

Activity ID	Activity Description	Orig Dur	MP1A w 3a Start	MP1A w 3a Finish	Current Start	Current Finish	% Comp	Total Float	Cal ID	2006				2007				2008				2009				2010																
										J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F

General & Preliminary

Commencement Date									
PRE-1020	Commencement of Works	0	18JUL06A		18JUL06A		100		2
Completion Date									
PRE-1060	Completion of Works	0		10NOV08		02JUL09	0	-192	2
General									
PRE-1040	Site Office Establishment	14	19JUL06A	31JUL06A	19JUL06A	31JUL06A	100		2

Manufacturing & Delivery

+ General									
		461	07AUG06A	10NOV07A	07AUG06A	10NOV07A	100		2

Instrumentation & Monitoring Works

+ General									
		899	18JUL06A	10NOV08	18JUL06A	02JUL09	81	505	1

Section 2a - Tunnel & Associated Works


Commencement Date									
2A-1020	Section Commencement	0	18JUL06A		18JUL06A		100		2
Completion Date									
2A-1040	Section Completion	0		10NOV08		30APR09	0	-129	2
+ Design & Submission									
		822	01AUG06A	14FEB08	01AUG06A		100		2
+ Soil Nail Works									
		628	12OCT06A	26NOV07	12OCT06A	31OCT08	99	44	1

High Tunnel

HT-C1020	Install Pipe Roof, Grouting & Temp. Soil Nails	21	27NOV06A	27JAN07A	27NOV06A	27JAN07A	100		1
HT-C1040	Construct Temporary Noise Enclosure	21	15DEC06A	28APR07A	15DEC06A	28APR07A	100		1
HT-C1060	Excavate Type A Tunnel (Soft)	45	30JAN07A	13MAR07A	30JAN07A	13MAR07A	100		1
HT-C1080	Excavate Type A Tunnel (Hard)	70	14MAR07A	31MAY07A	14MAR07A	31MAY07A	100		1
HT-C1100	Excavate Low Tunnel Chamber	45	24APR07A	06AUG07A	24APR07A	06AUG07A	100		1
HT-C1110	1st Site Trials of Sub-vert. Drain	2	16JUL07A	27JUL07A	16JUL07A	27JUL07A	100		1
HT-C1120	Excavate Type B2 Starter Tunnel	50	02JUN07A	14JUL07A	02JUN07A	14JUL07A	100		1
HT-C1140	Level & Setup Rail & Track to TBM Excavation	50	09JUL07A	28AUG07A	09JUL07A	28AUG07A	100		1
HT-C1160	Install & T&C of Mucking System	90	26MAR07A	18SEP07A	26MAR07A	18SEP07A	100		1
HT-C1180	Assembly TBM at Portal & Move into High Tunnel	30	10AUG07A	18SEP07A	10AUG07A	18SEP07A	100		1
HT-C1200	Excavate High Tunnel(TBM)(Grouting Allowed)	30	19SEP07A	01DEC07	19SEP07A	08DEC07A	100		1
HT-C1220	Retract TBM & Remove from High Tunnel	14	03DEC07	18DEC07	10DEC07A	27DEC07A	100		1
HT-C1240	Cast Invert of Type B Tunnel (259m)	45	19DEC07	24JAN08	23JUL08A	29OCT08A	100		1
HT-C1260	Remaining Site Trials of Sub-vert. Drains	2	25JAN08	26JAN08	03JAN08A	05JAN08A	100		1
HT-C1280	Install Sub-vert. Drains (99 nos.)	120	28JAN08	07APR08	28DEC07A	22JUL08A	100		1
HT-C1290	Cast Invert of Type A Tunnel (U0+00~U0+22.5)	14	28JAN08	07APR08	10OCT08A	15OCT08A	100		1
HT-C1300	Cast Type B Crown Lining (259m),Drains,etc	60	08APR08	05JUN08	18AUG08A	12NOV08	99	-91	1
HT-C1305	Construct Headwalls at Intersection	6			15JAN09	21JAN09	0	-85	1
HT-C1310	Erection of Type A Crown Lining Formwork	18			13NOV08	03DEC08	0	-91	1
HT-C1320	Cast Type A Crown Lining (U0+00~U0+22.5)	40	06JUN08	22AUG08	04DEC08	21JAN09	0	-91	1
HT-C1325	Lining Design Confirmation (U0+22.5~U0+37.5)	0			31OCT08*		0	505	1
HT-C1330	Cast Invert of Type A Tunnel (U0+22.5~U0+37.5)	18			25SEP08A	09OCT08A	100		1
HT-C1332	Mobilization & Site Trial	10			06FEB09	17FEB09	0	-91	1
HT-C1335	Shotcrete Type A Crown Lining (U0+22.5~U0+37.5)	20			18FEB09	12MAR09	0	-91	1
HT-C1340	Cast Vertical Shaft, Walkway & Drainage	25	23AUG08	23SEP08	13MAR09	10APR09	0	-91	1
HT-C1360	Complete Sub-vert. Drain Connection,Downpipe,etc	60	08AUG08	17OCT08	13NOV08	23JAN09	0	-26	1
HT-C1380	E&M Works & External Works	60	14AUG08	10NOV08	20FEB09	30APR09	0	-102	1

Low Tunnel


LT-C1020	Excavate Type B2 Starter Tunnel (15m)	70	07AUG07A	22OCT07A	07AUG07A	22OCT07A	100		1
LT-C1040	Reposition TBM for Low Tunnel Excavation	14	19DEC07	05JAN08	28DEC07A	26FEB08A	100		1
LT-C1060	Excavate Low Tunnel(TBM-165m)(Grouting Allowed)	14	07JAN08	22JAN08	26FEB08A	17MAR08A	100		1
LT-C1080	Remove TBM & Track from Low Tunnel	14	23JAN08	07FEB08	18MAR08A	31MAR08A	100		1
LT-C1100	Remove Hopper & Conveyor System	30	08FEB08	13MAR08	18MAR08A	31JUL08A	100		1
LT-C1120	Cast Invert of Type B Tunnel (179m)	20	14MAR08	07APR08	13NOV08	05DEC08	0	-61	1

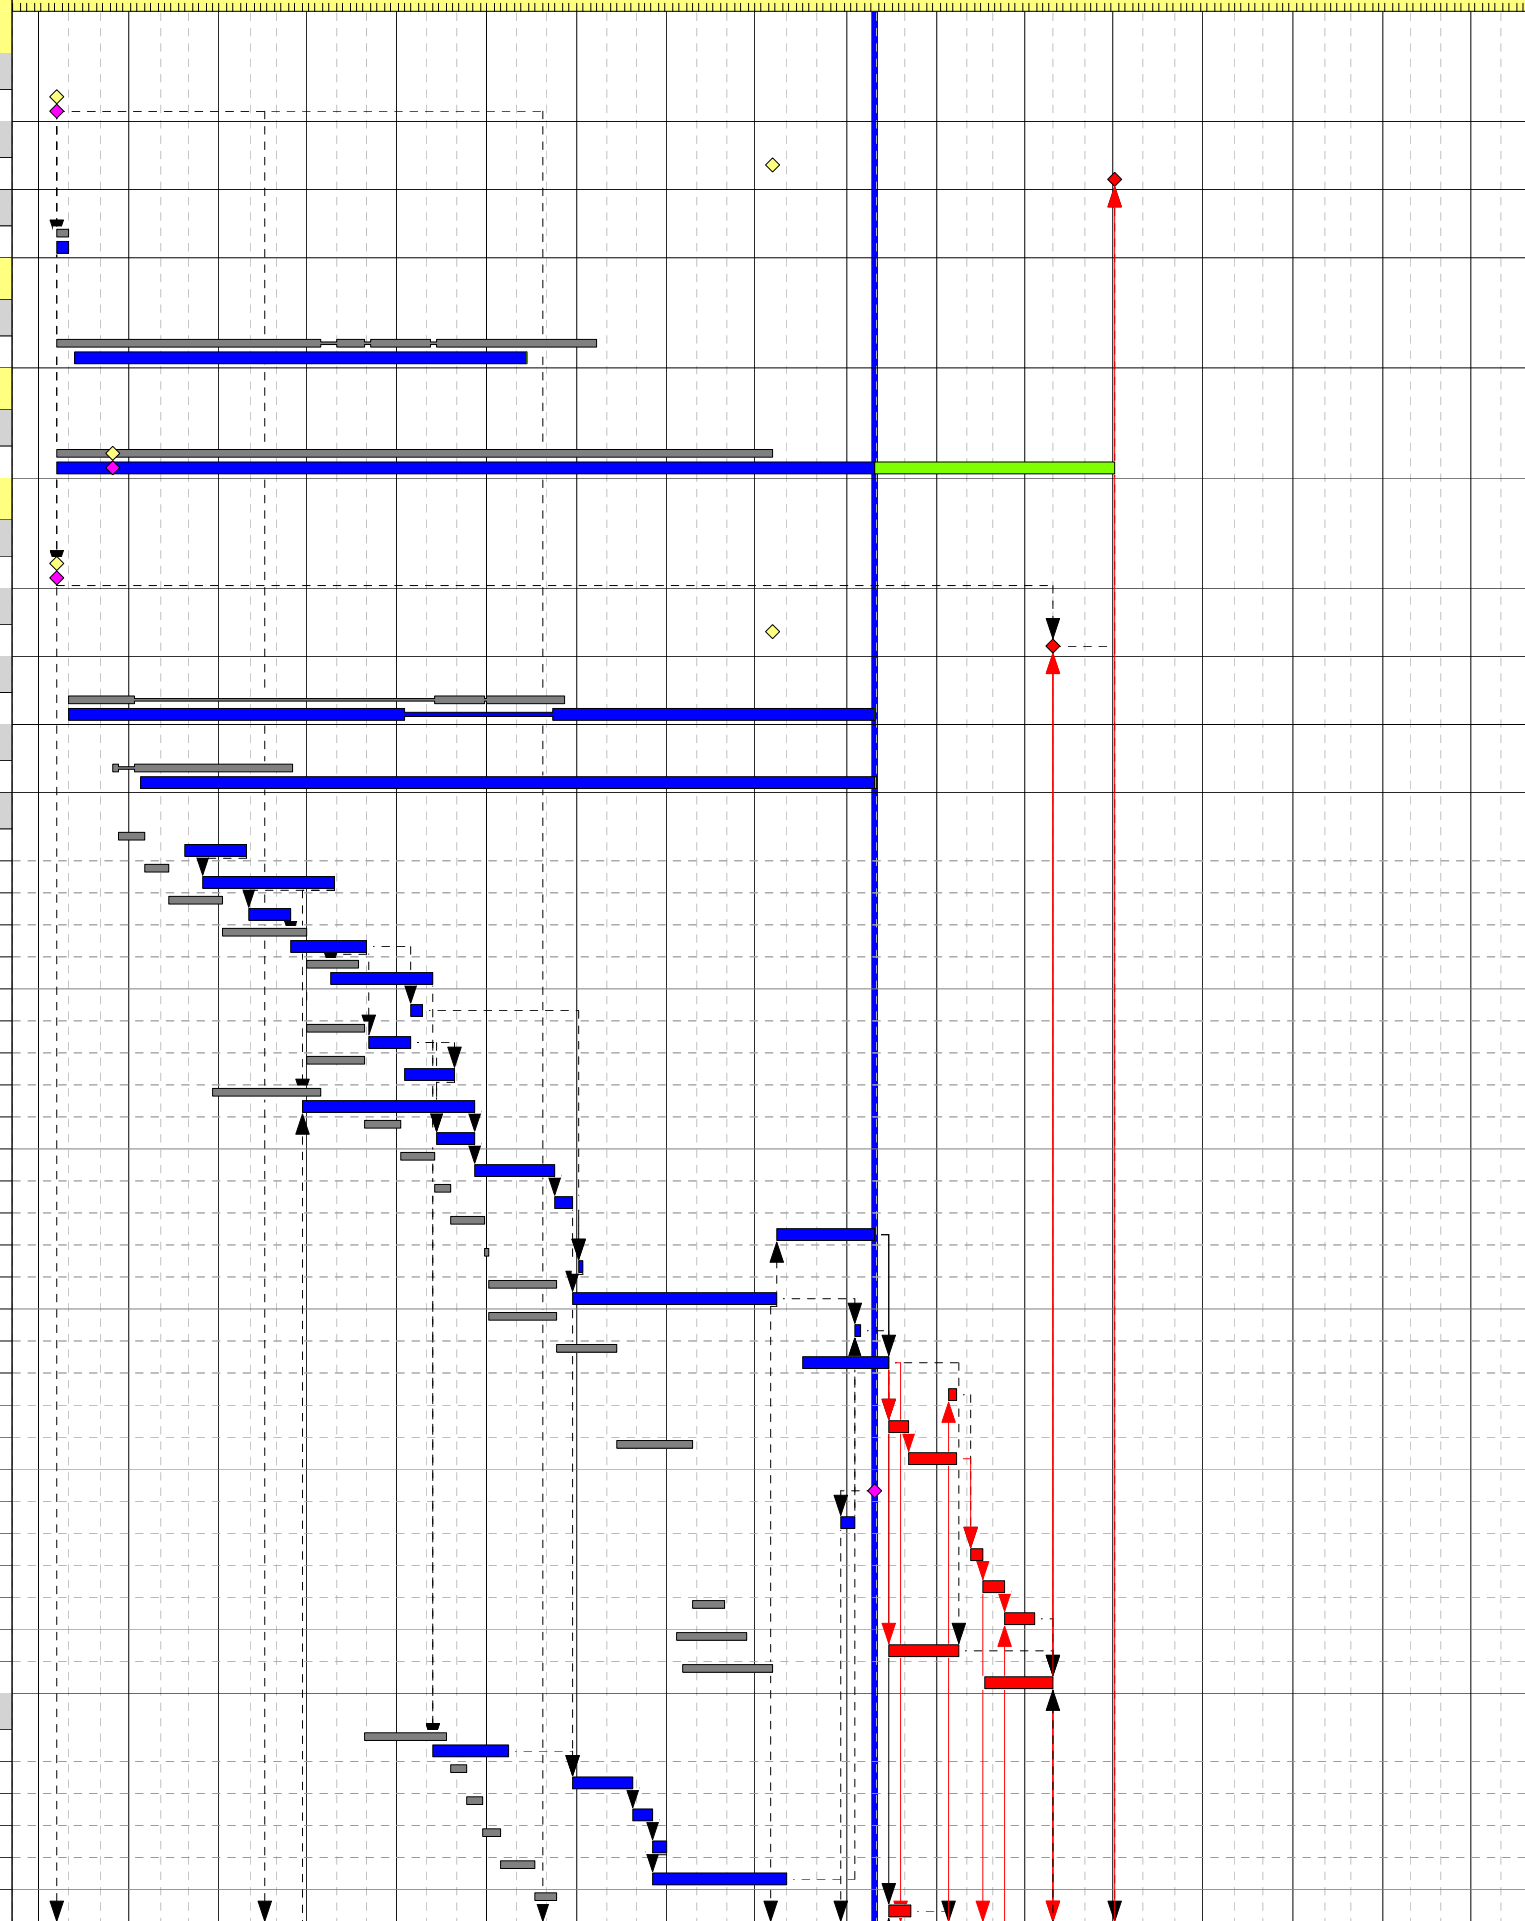

Start Date 04JUL06
 Finish Date 02JUL10
 Data Date 31OCT08
 Run Date 03NOV08 09:09

MP1A	MP1A
Current	Current
Progress Bar	Progress Bar
Critical Activity	Critical Activity

MP27
 Contract GE/2005/45
 Landslide Preventive Works
 at Po Shan Road, Mid-Levels
 (as at 31 Oct 2008)
 Monthly Progress Update



Revisions			
Date	Revision	Checked	Approved
31OCT08	For Monthly Progress Report (MP27)	CYM	ET

