



生興 - 豐利聯營
Sang Hing - Kuly Joint Venture

28th June 2019

Our ref.: SKJV/W52/SO/3497

Mannings (Asia) Consultants Ltd.
5/F, Winning Commercial Building,
46-48 Hillwood Road,
Tsim Sha Tsui,
Kowloon

By fax & post
Fax no.: 3168 2022

Attn.: Mr. Mole Tam (Senior Resident Engineer)

Dear Sirs,

Contract No. YL/2015/01

**Cycle Tracks from Tuen Mun to Sheung Shui – Remaining Works
Updated Programme**

Enclosed please find our updated programme for your information and acceptance. A summary is also attached herewith this letter for your easy reference.

In several meetings, we understand that CEDD and your Office would request us to complete the proposed Cycle Track by the end of this year. However, our programme are hindered by some external constraints such as Street Lighting Works by Highways Department, approval of GRP Roofing at Subway A & D, utilities diversions at Retaining Walls RW49 and RW50 and additional walls at Portions J1 to J3, etc.

In view of this requirement, we would like to arrange an ad hoc meeting to seek a better solution to accelerate the works.

Thank you for your kind attention

Yours faithfully,
For and on behalf of
Sang Hing - Kuly Joint Venture

Tang Wing Kai
Site Agent

WKT/MKM/TL/tl

Encl.


Section	Portion	Revised Completion Date	Revised Completion Date (Including with Time Saving)	Updated Programme Completion Date	Major outstanding work / critical work	Target Completion	Critical Priority	Remark
W1	A			30/9/2019	1) Street Lighting works and Colour Dressing	30-Sep-19		
					1) Subway A Bay 12 to Bay 16	16-Oct-19		
	B	5/6/2019	7/4/2019	23/2/2020	2) GRP Roofing Approval	15-Jul-19	2nd	Assume GRP approval obtained on 15/7/19
					3) GRP Roofing Order and Delivery	15-Oct-19		
					4) GRP installation	13-Jan-20		
					5) Road work inside subway	23-Feb-20		
					5) Street Lighting works and colour Dressing	30-Sep-19		
	C			11/7/2019	1) Street Lighting works and Colour Dressing	7-Nov-19		
					2) Additional Proposed staircase, ramp at Yau Po Road	16-Oct-19		
	D			15/4/2020	1) Approval of Street Lighting	30-Jun-19	1st	
					2) Allocation Warrant and Installation of Street Lighting	6-Mar-20		
					3) Colour Dressing	15-Apr-20		

W2	E	15/4/2020	1) Retaining Wall RW D03	26-Mar-20	3rd	Assume Approval given on 30 June 2019
			2) Approval of Street Lighting	30-Jun-19	2nd	
			3) Allocation Warrant and Installation of Street Lighting	6-Mar-20		
			4) Colour Dressing	15-Apr-20		
	F	15/4/2020	1) RW 42 (CSD)	30-Dec-19	3rd	Assume Approval given on 30 June 2019
			2) RW 44 and Ramp PR3	19-Dec-19		
			3) Approval of Street Lighting	30-Jun-19	2nd	
			4) Allocation Warrant and Installation of Street Lighting	6-Mar-20		
			5) Colour Dressing	15-Apr-20		
	G	31/3/2020	1) Approval of Street Lighting	30-Jun-19	2nd	Assume Approval given on 30 June 2019
			2) Allocation Warrant and Installation of Street Lighting	6-Mar-20		
			3) Colour Dressing	31-Mar-20		
	H	25/4/2021	1) Additional RW49 & RW50	10/2/2020	1st	
			2) Additional Diversion of utilities along RW49 & RW50	8/8/2020		
			3) Drainage and Gullies for re-alignment carriageway for RW49 & RW50	7/10/2020		
			4) Road Works for re-alignment of DW1 and DW2 and street lighting works	25/4/2021		
	I	13/3/2020	1) Subway D E&M works	1-Nov-19	2nd	Assume GRP approval obtained on 15/7/19
			2) GRP Roofing Approval	15-Jul-19		
			3) GRP Roofing Order and Delivery	15-Oct-19		
			4) GRP installation	13-Jan-20		
			5) Road work inside subway	13-Mar-20		
	N	20/3/2020	1) Bridge B - Substructure	30-Sep-19	3rd	Assume Approval given on 30 June 2019
			2) Bridge B - Superstructure	30-Nov-19		
			3) Bridge B - Site formation	20-Jan-20		
			4) Approval of Street Lighting	30-Jun-19	2nd	
			5) Allocation Warrant and Installation of Street Lighting	6-Mar-20		
			6) Colour Dressing	20-Mar-20		


W3	K&J1	30/5/2019	1/4/2019	5/4/2020	1) Approval of Street Lighting	30-Jun-19	1st	Assume Approval given on 30 June 2019
					2) Allocation Warrant and Installation of Street Lighting	6-Mar-20		
					3) Colour Dressing	5-Apr-20		


W5	M	11/9/2019	11/9/2019	31/3/2020	1) Steel roofing and E&M of Bridge E	27-Dec-19		
					2) Approval of Street Lighting	30-Jun-19	1st	Assume Approval given on 30 June 2019
					3) Allocation Warrant and Installation of Street Lighting	6-Mar-20		
					4) Colour Dressing	31-Mar-20		

W7	J1,J2,J3	14/6/2019	16/4/2019	20/4/2020	1) RW48, RW24A, RW24AA, etc	31-Dec-19	1st	
					2) Earthwork and Drainage works	29-Feb-20		
					3) Road Work (except colour dressing)	30-Mar-20		
					2) Approval of Street Lighting	30-Jun-19		
					3) Allocation Warrant and Installation of Street Lighting	6-Mar-20	2nd	Assume Approval given on 30 June 2019
					4) Colour Dressing	24-Apr-20		

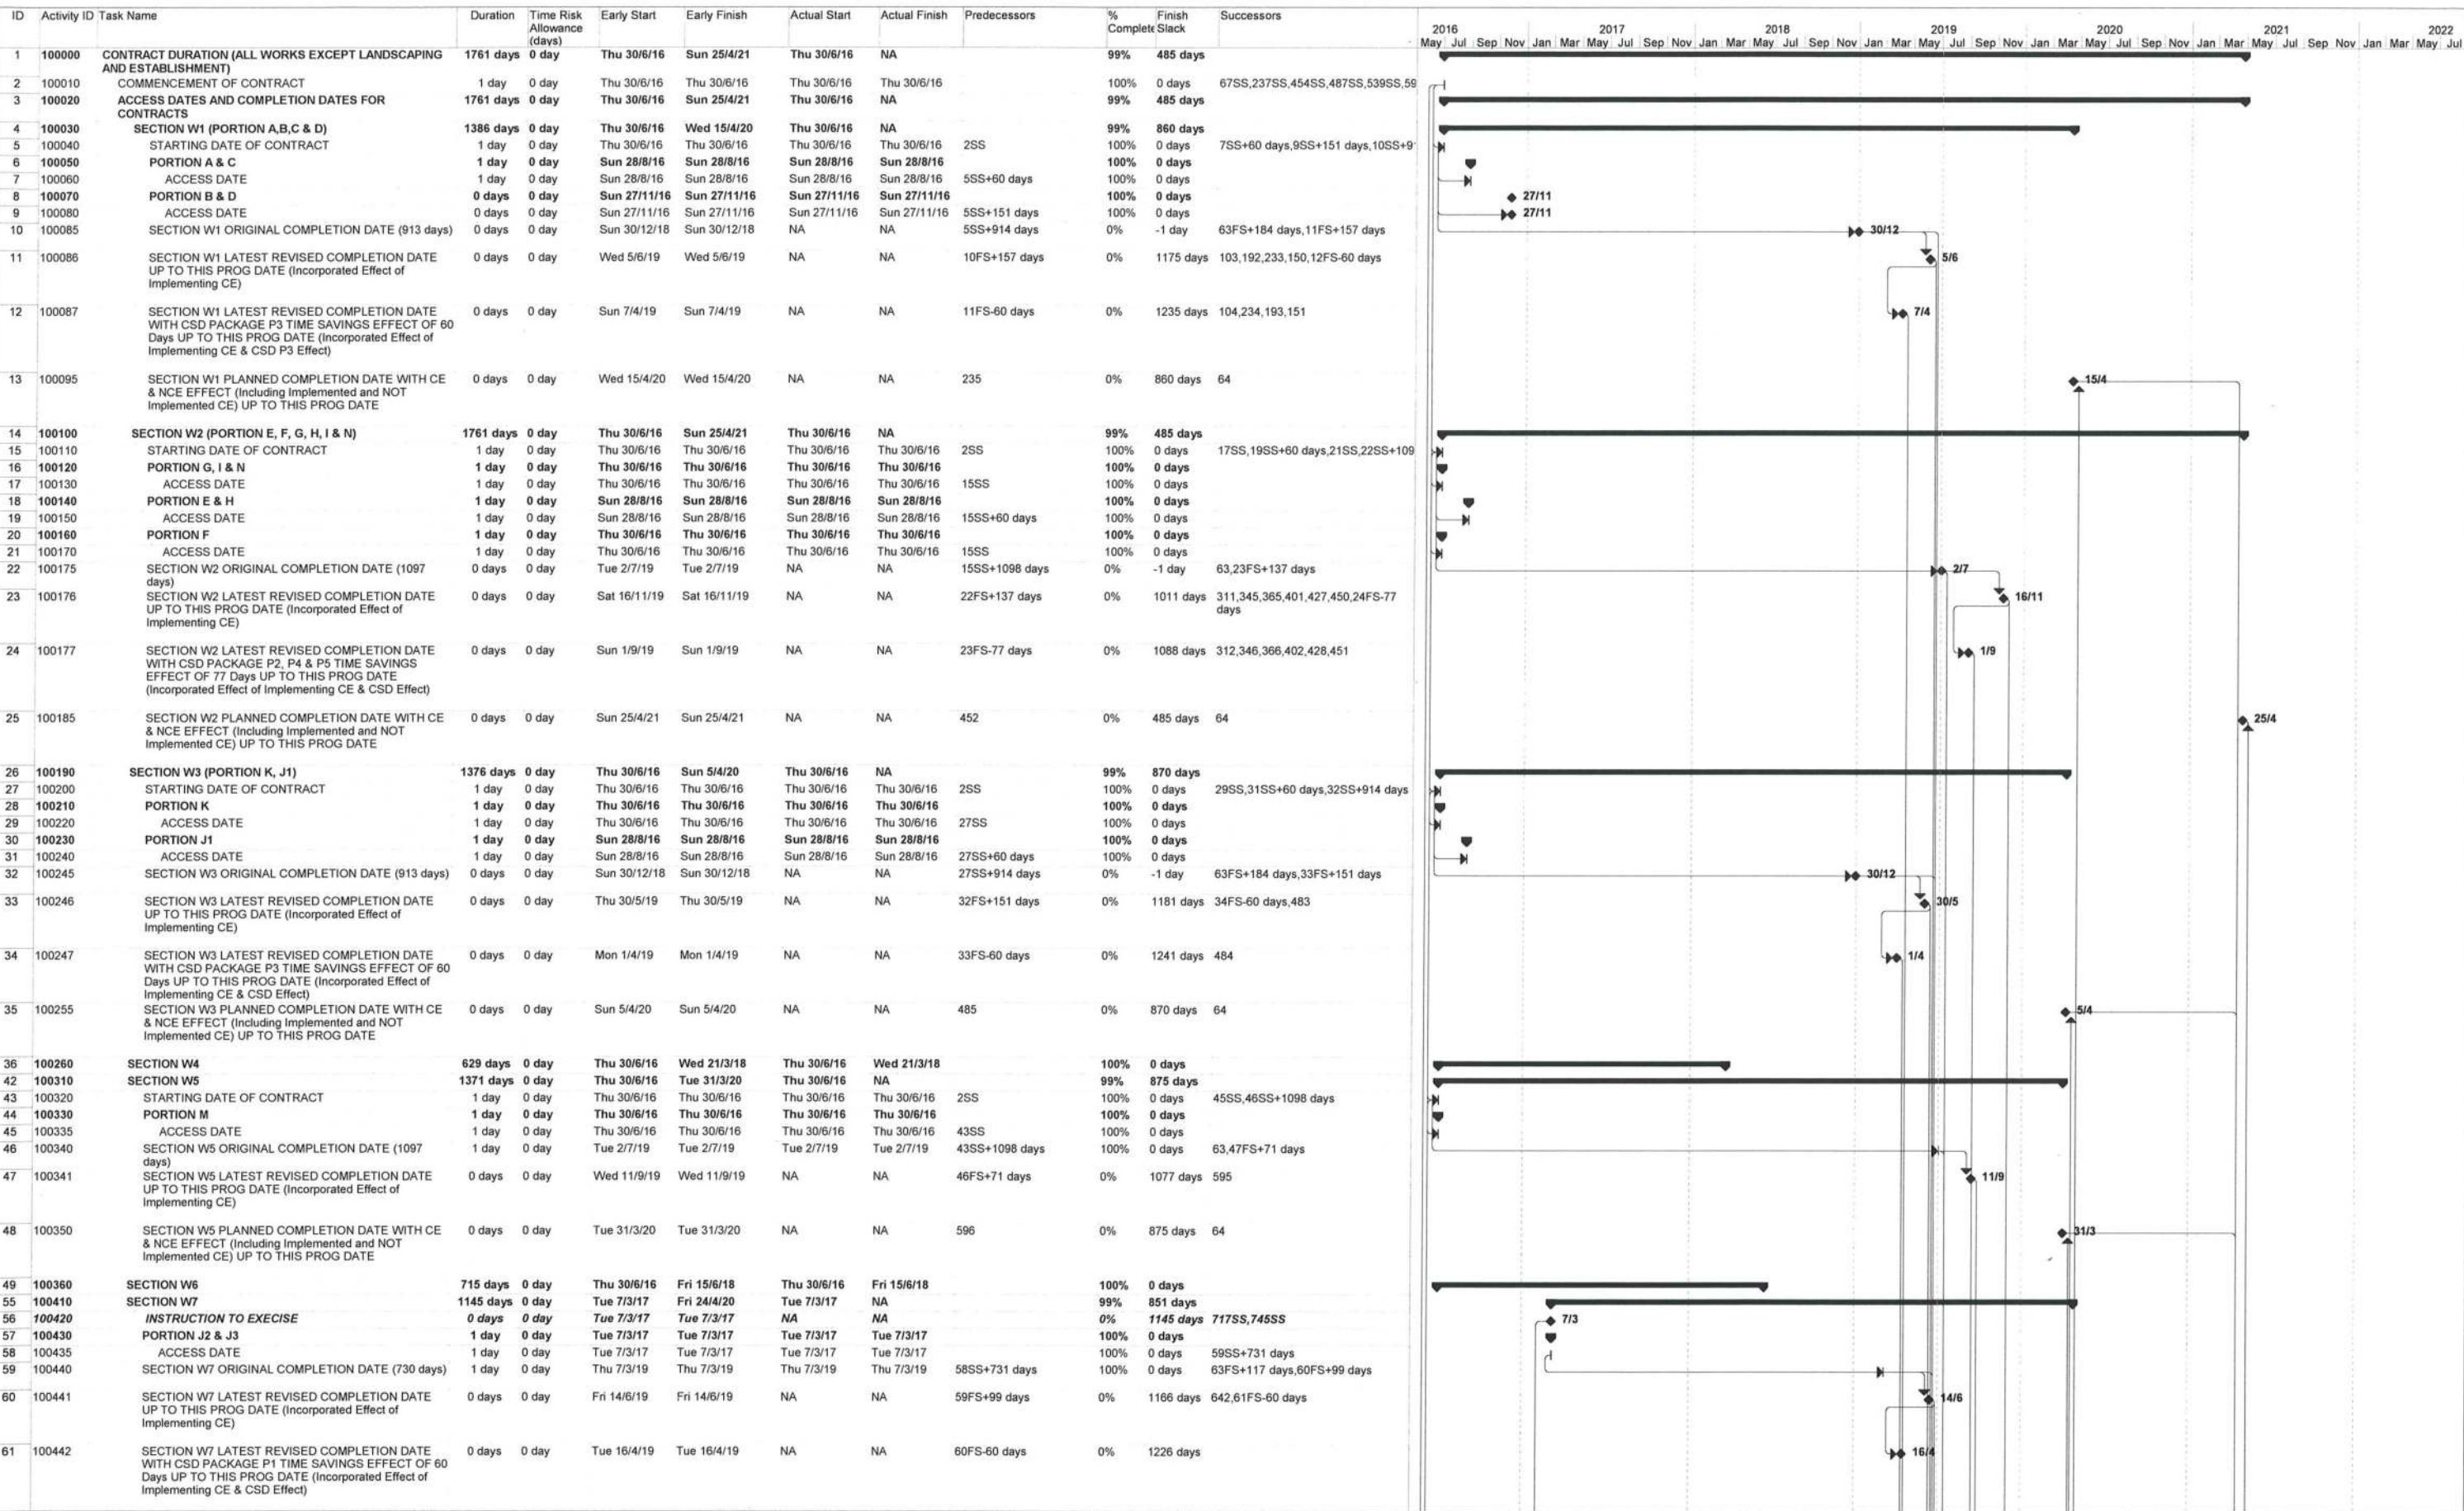



REMARK: ALL SUNDAYS AND HOLIDAYS ARE INCLUDED IN THIS PROGRAMME

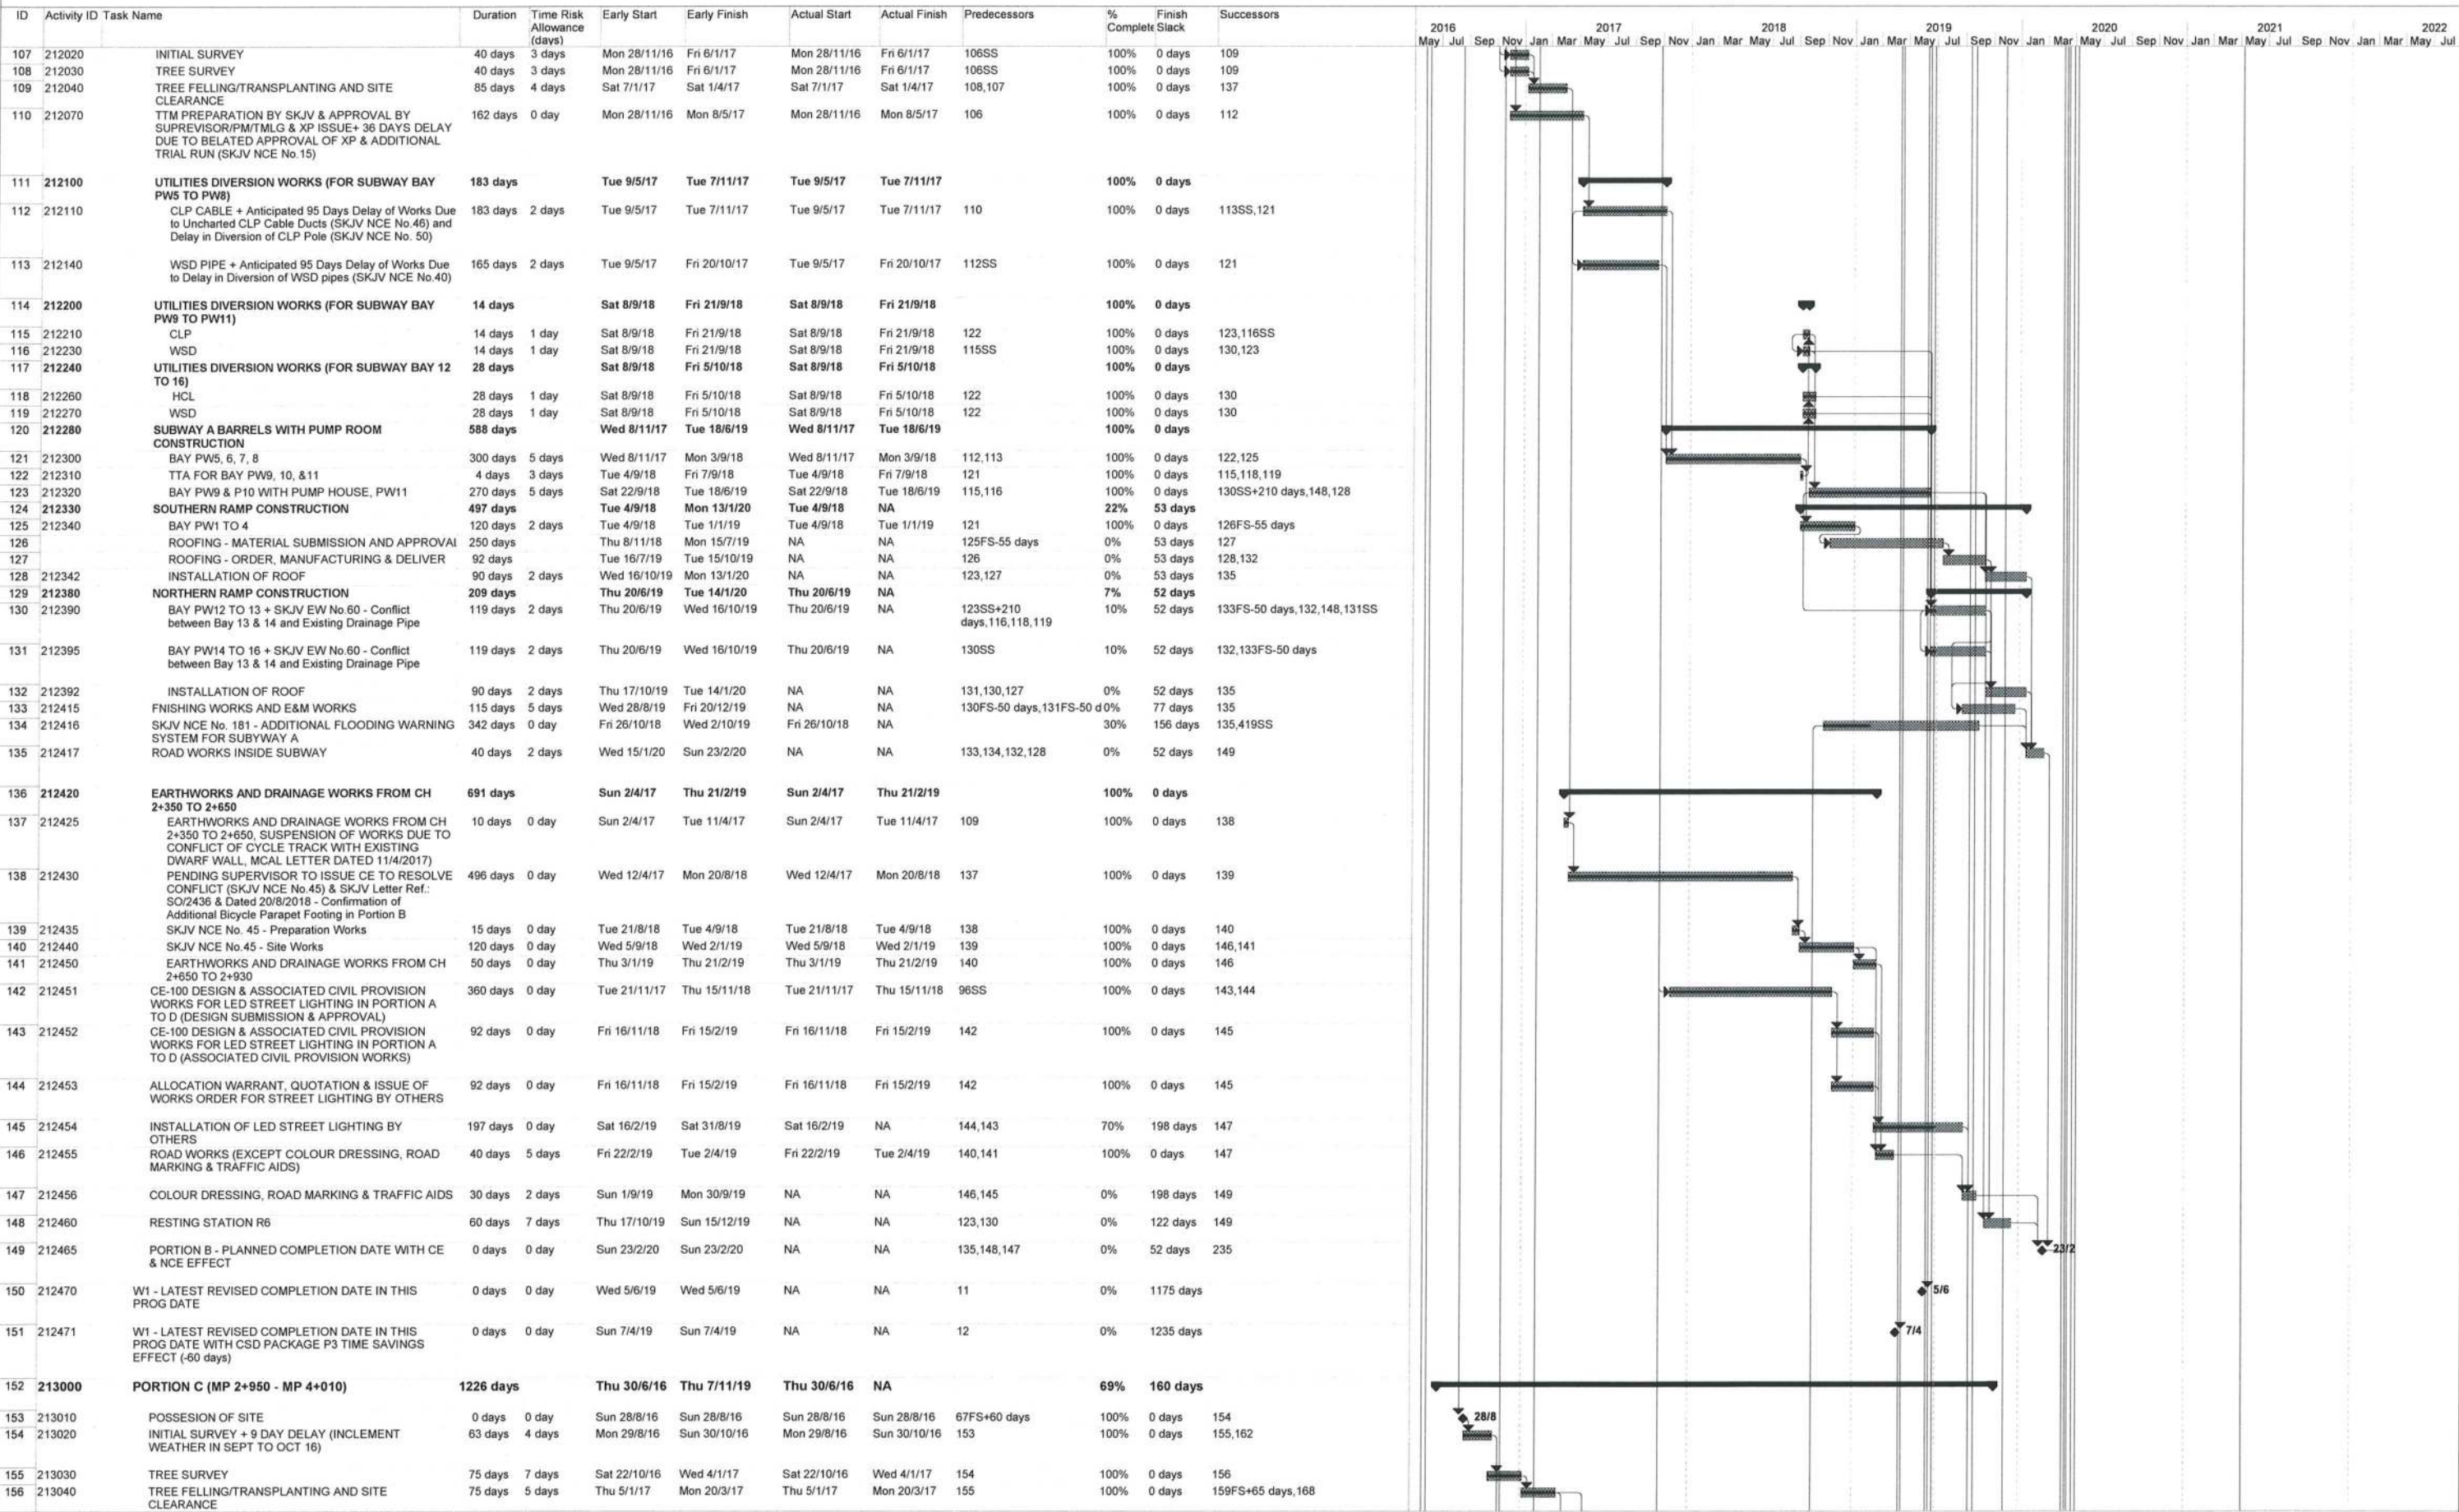

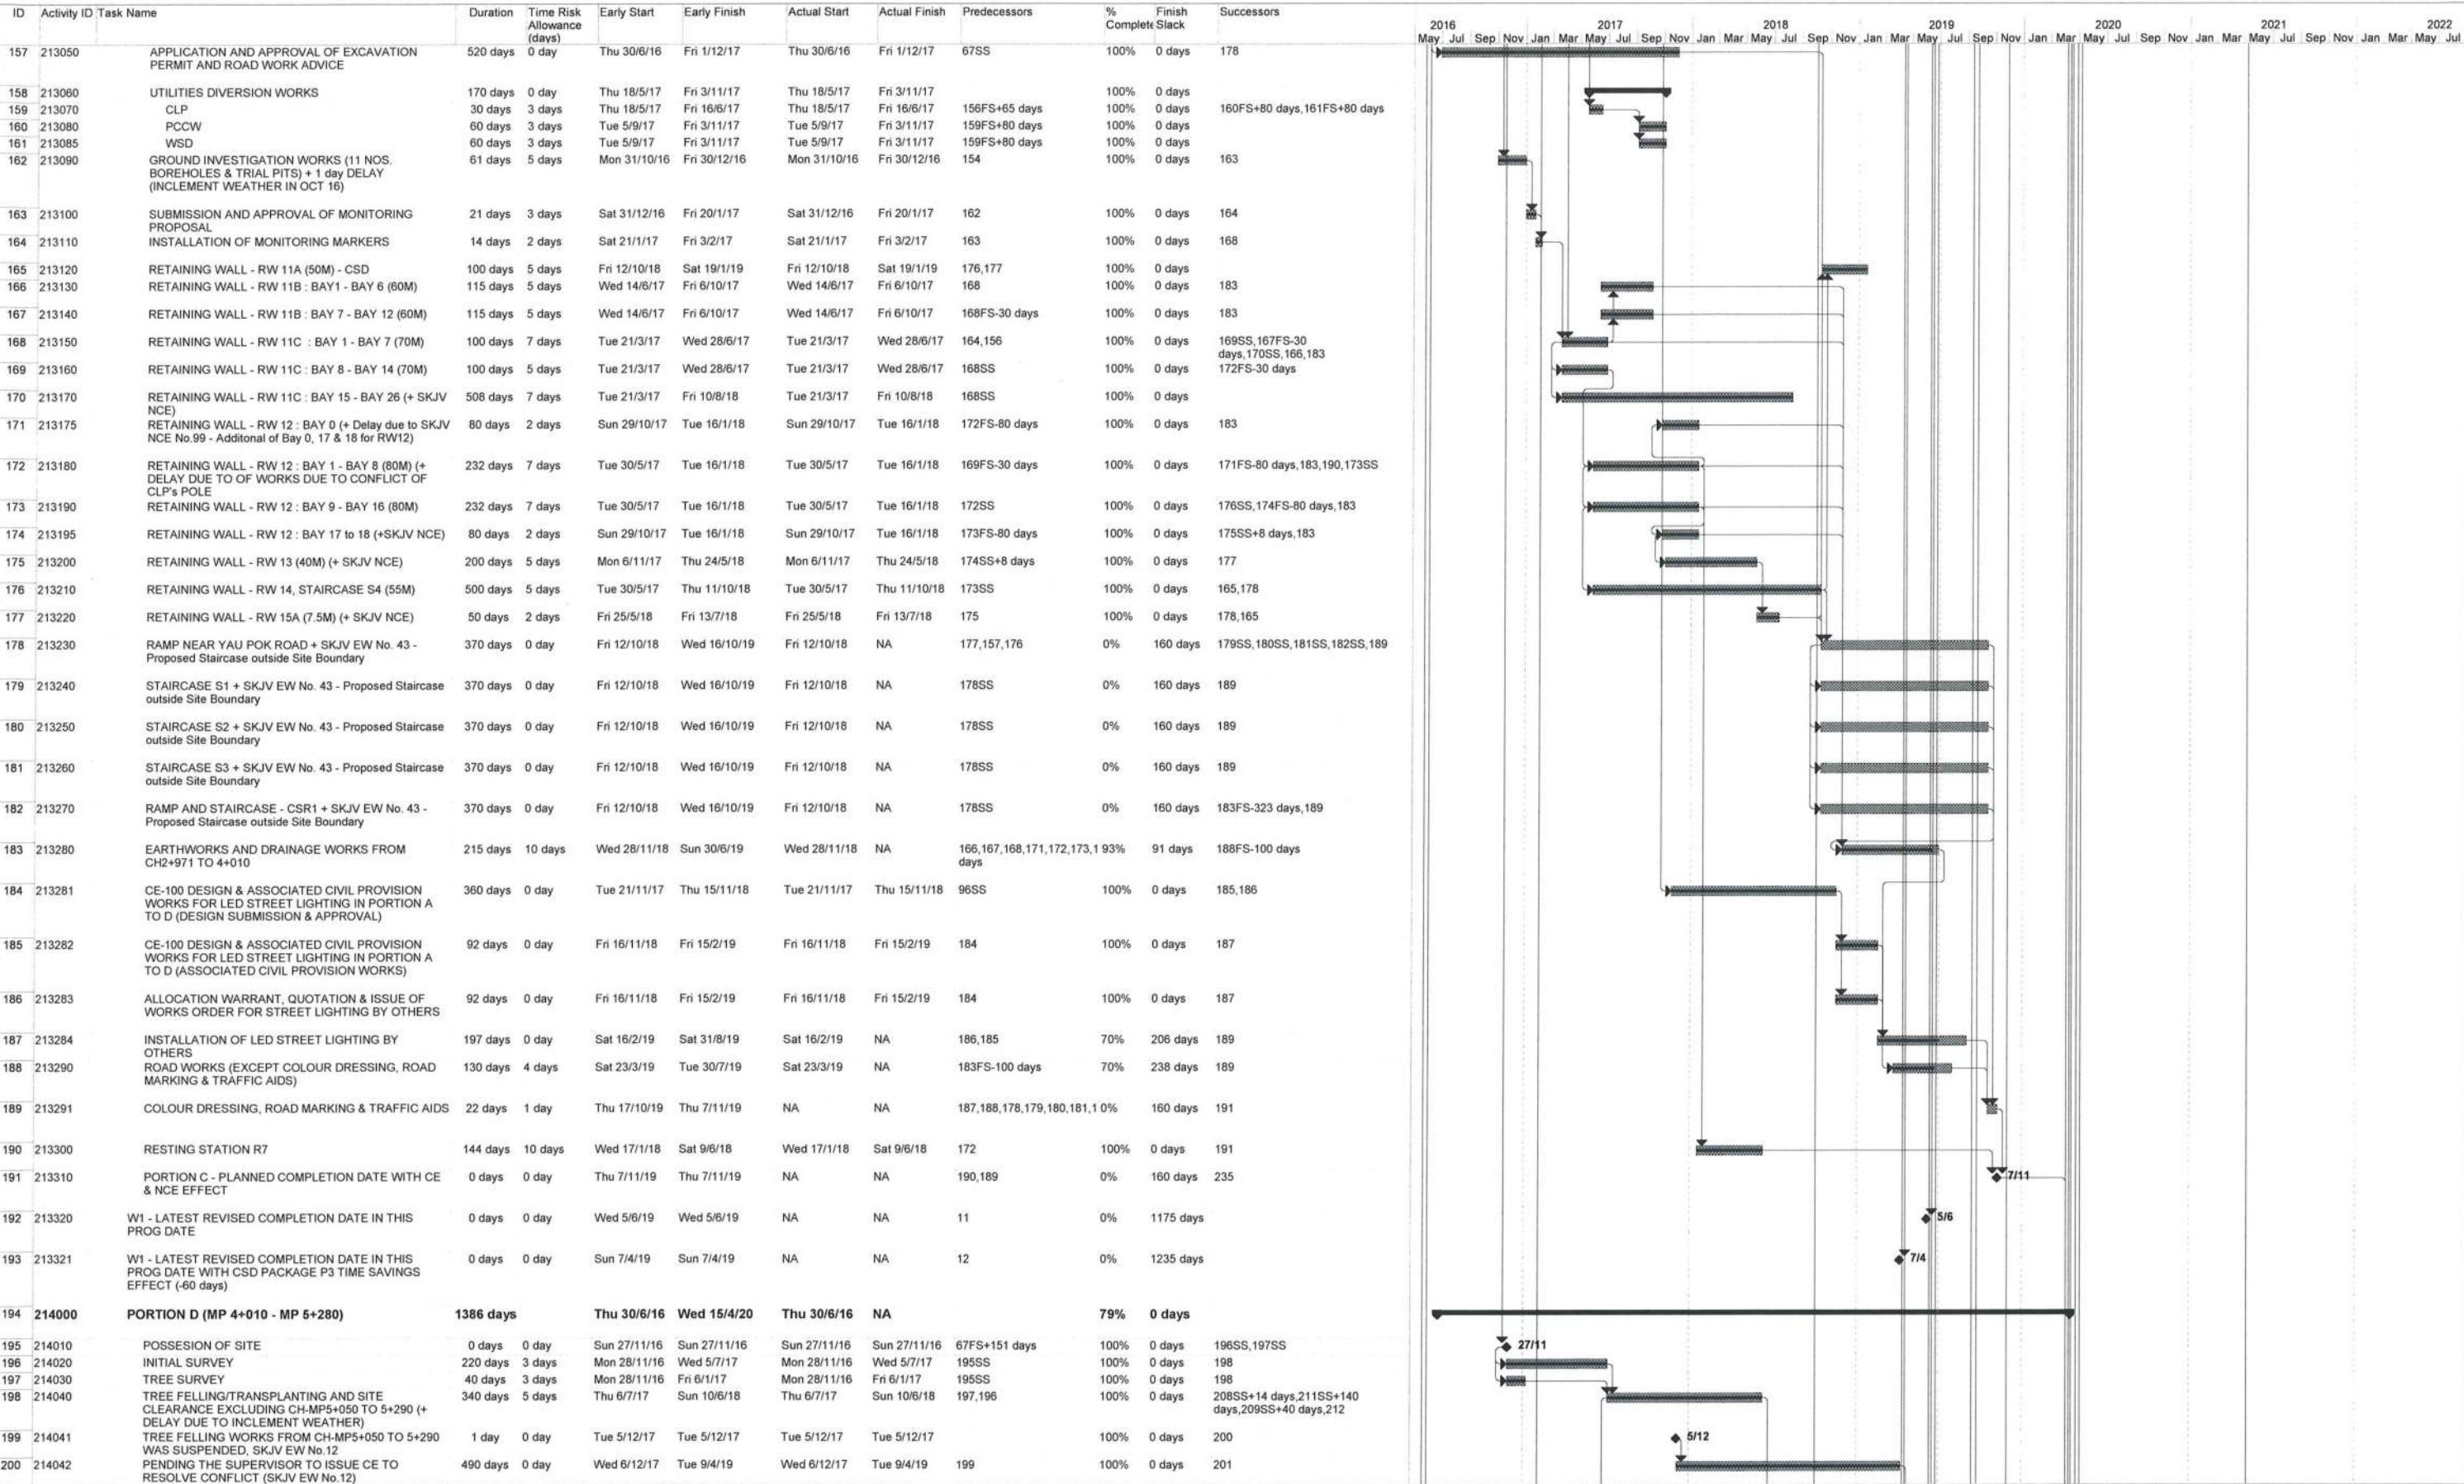


REMARK: ALL SUNDAYS AND HOLIDAYS ARE INCLUDED IN THIS PROGRAMME

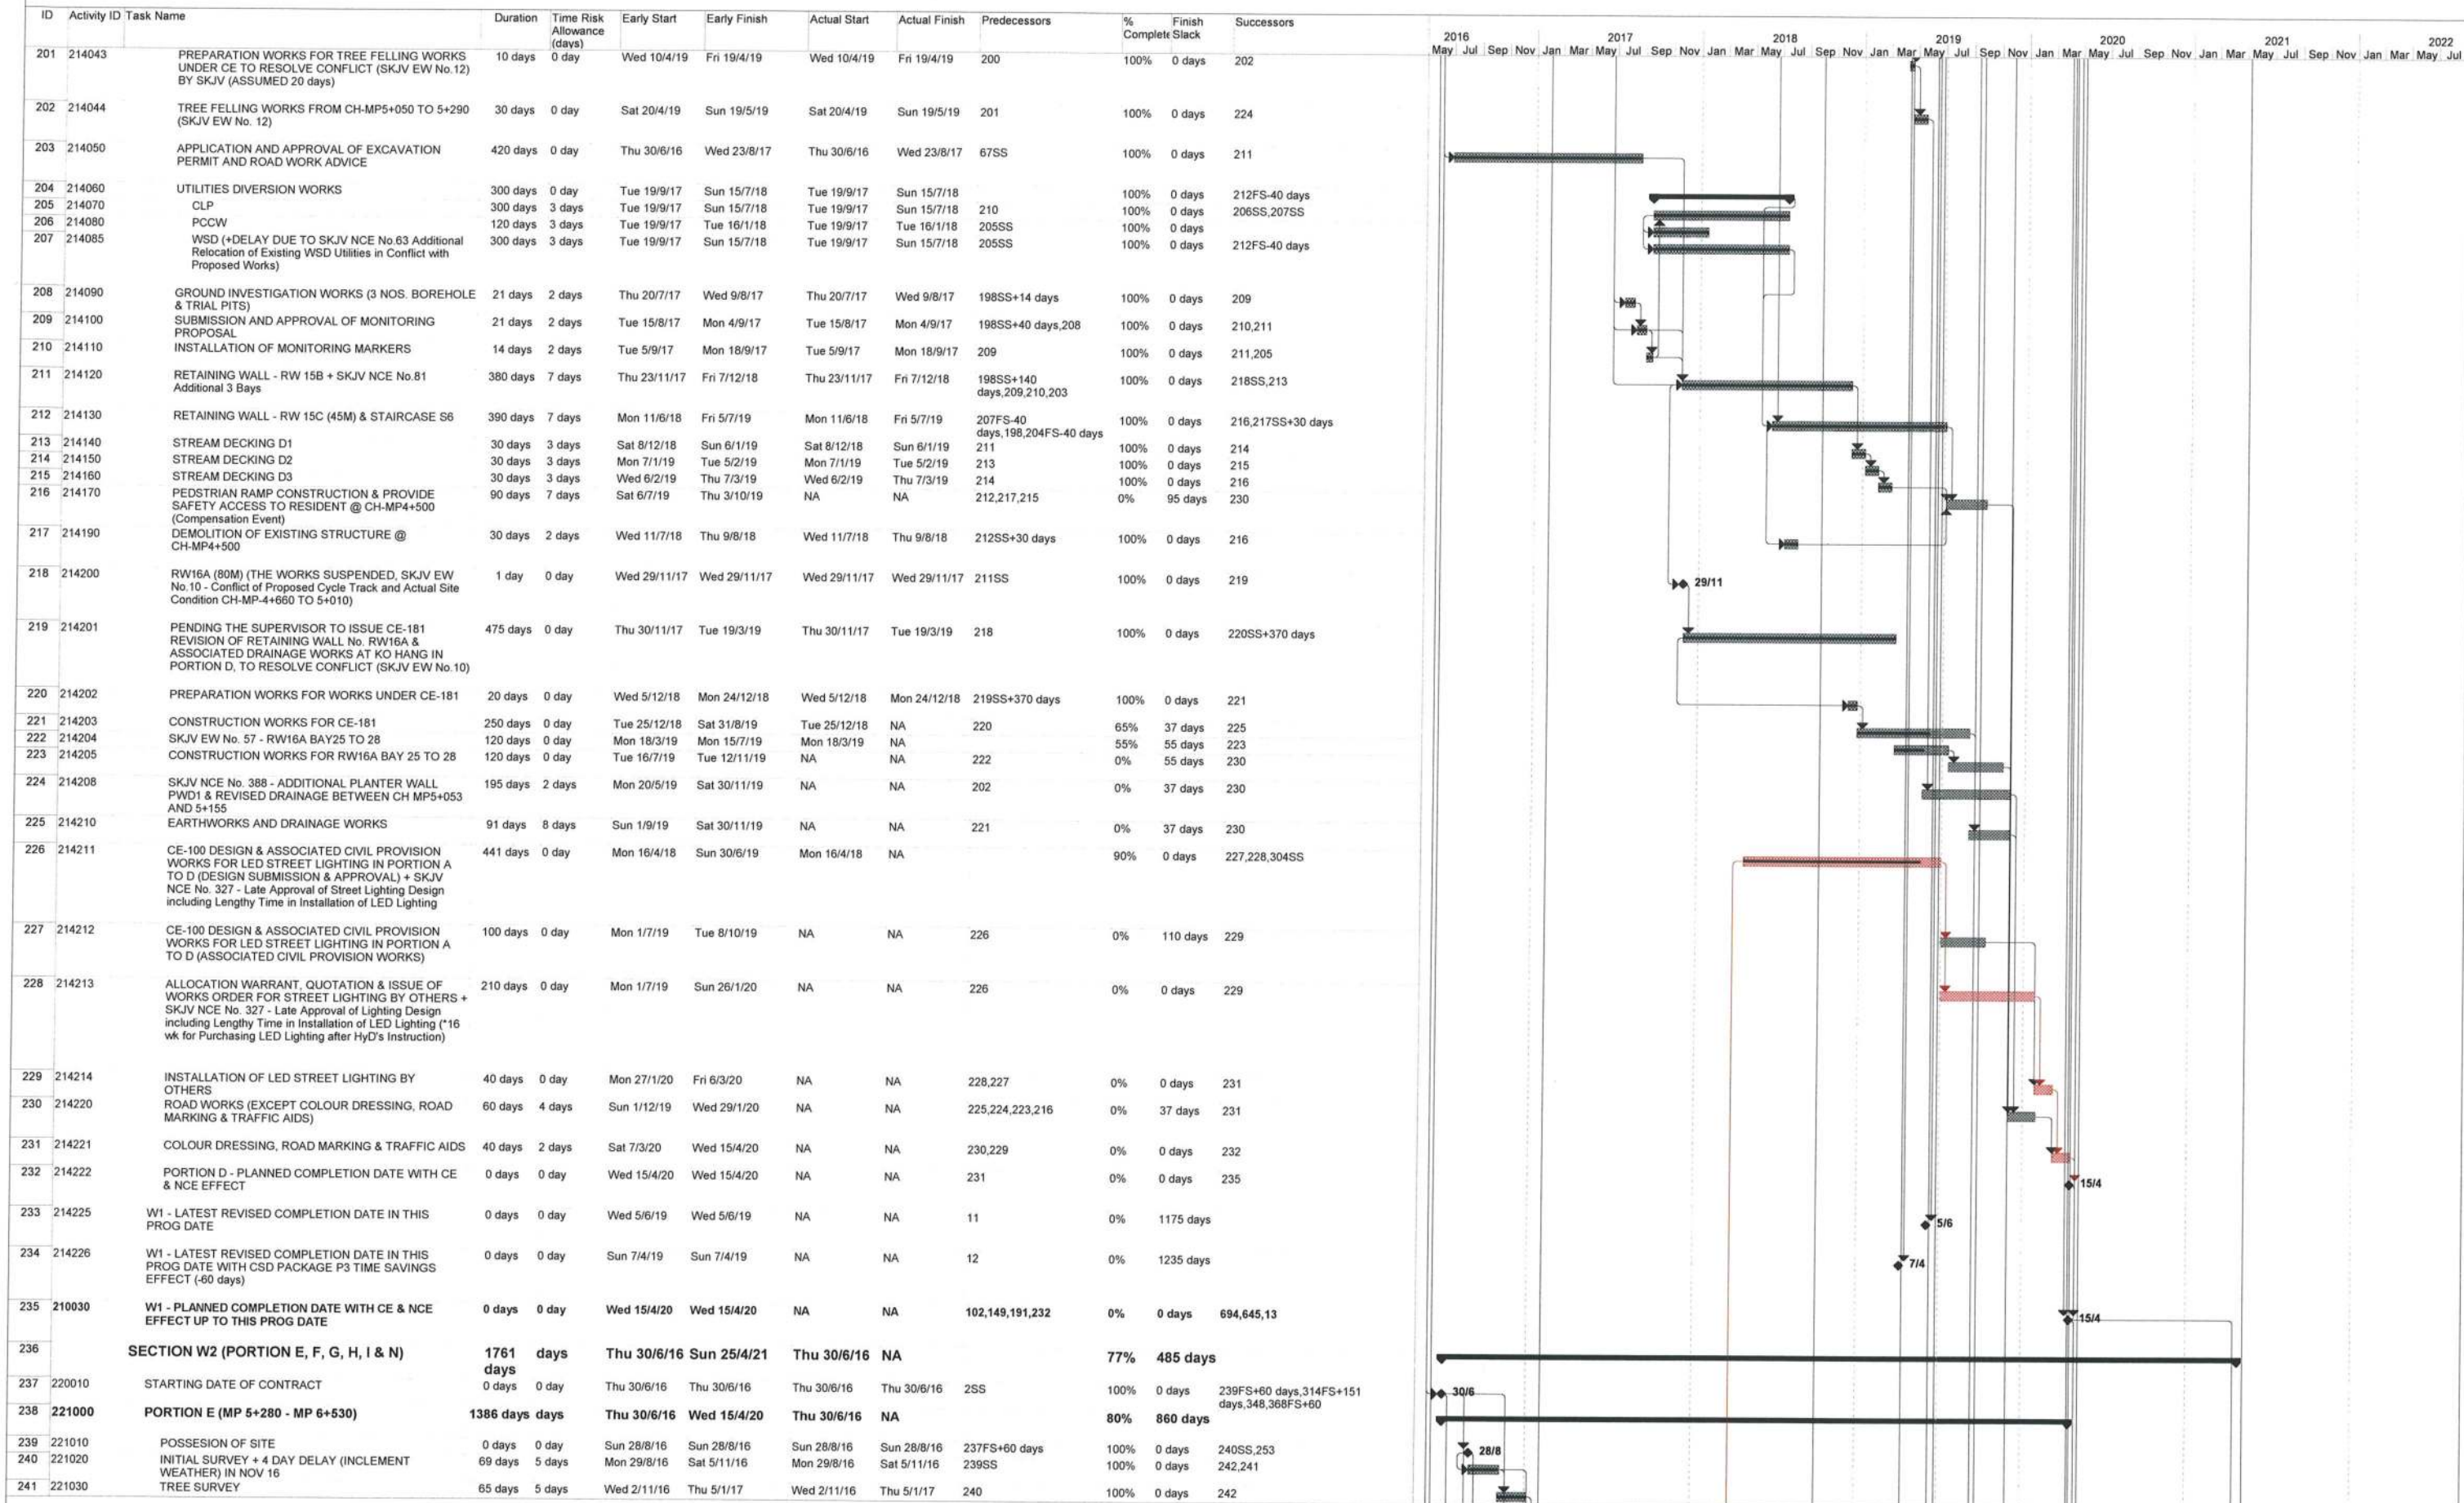

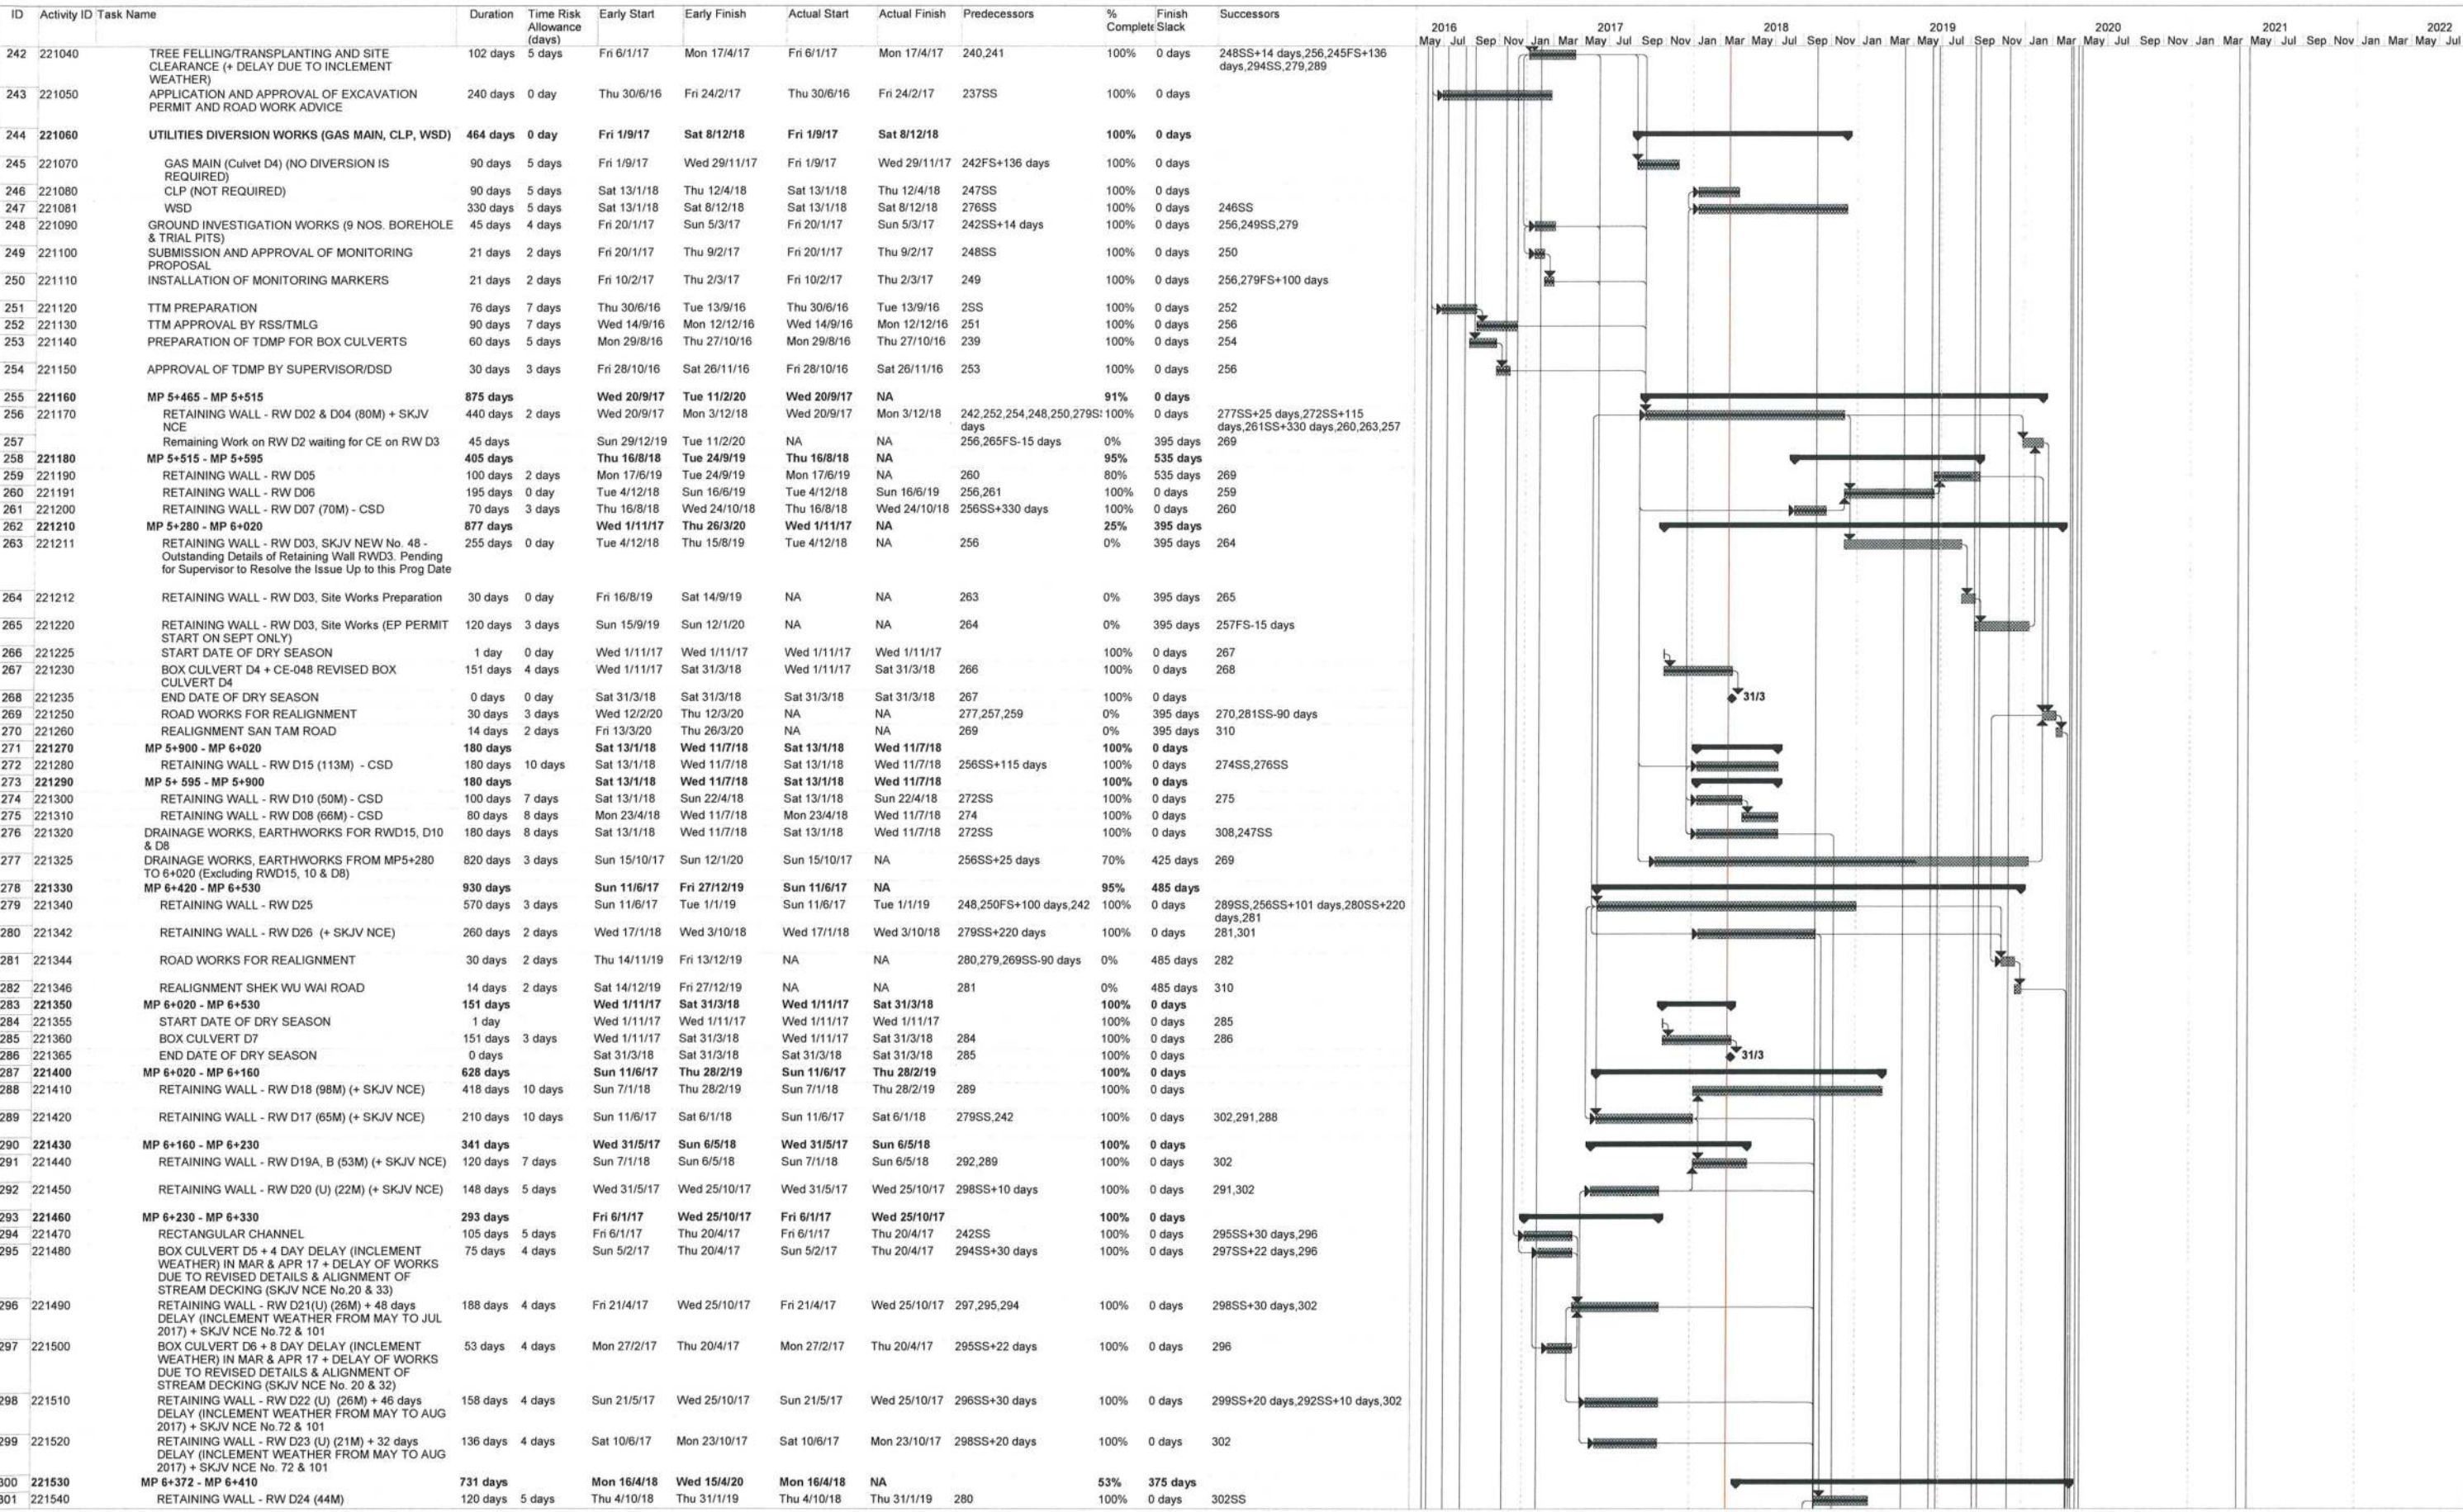


REMARK: ALL SUNDAYS AND HOLIDAYS ARE INCLUDED IN THIS PROGRAMME

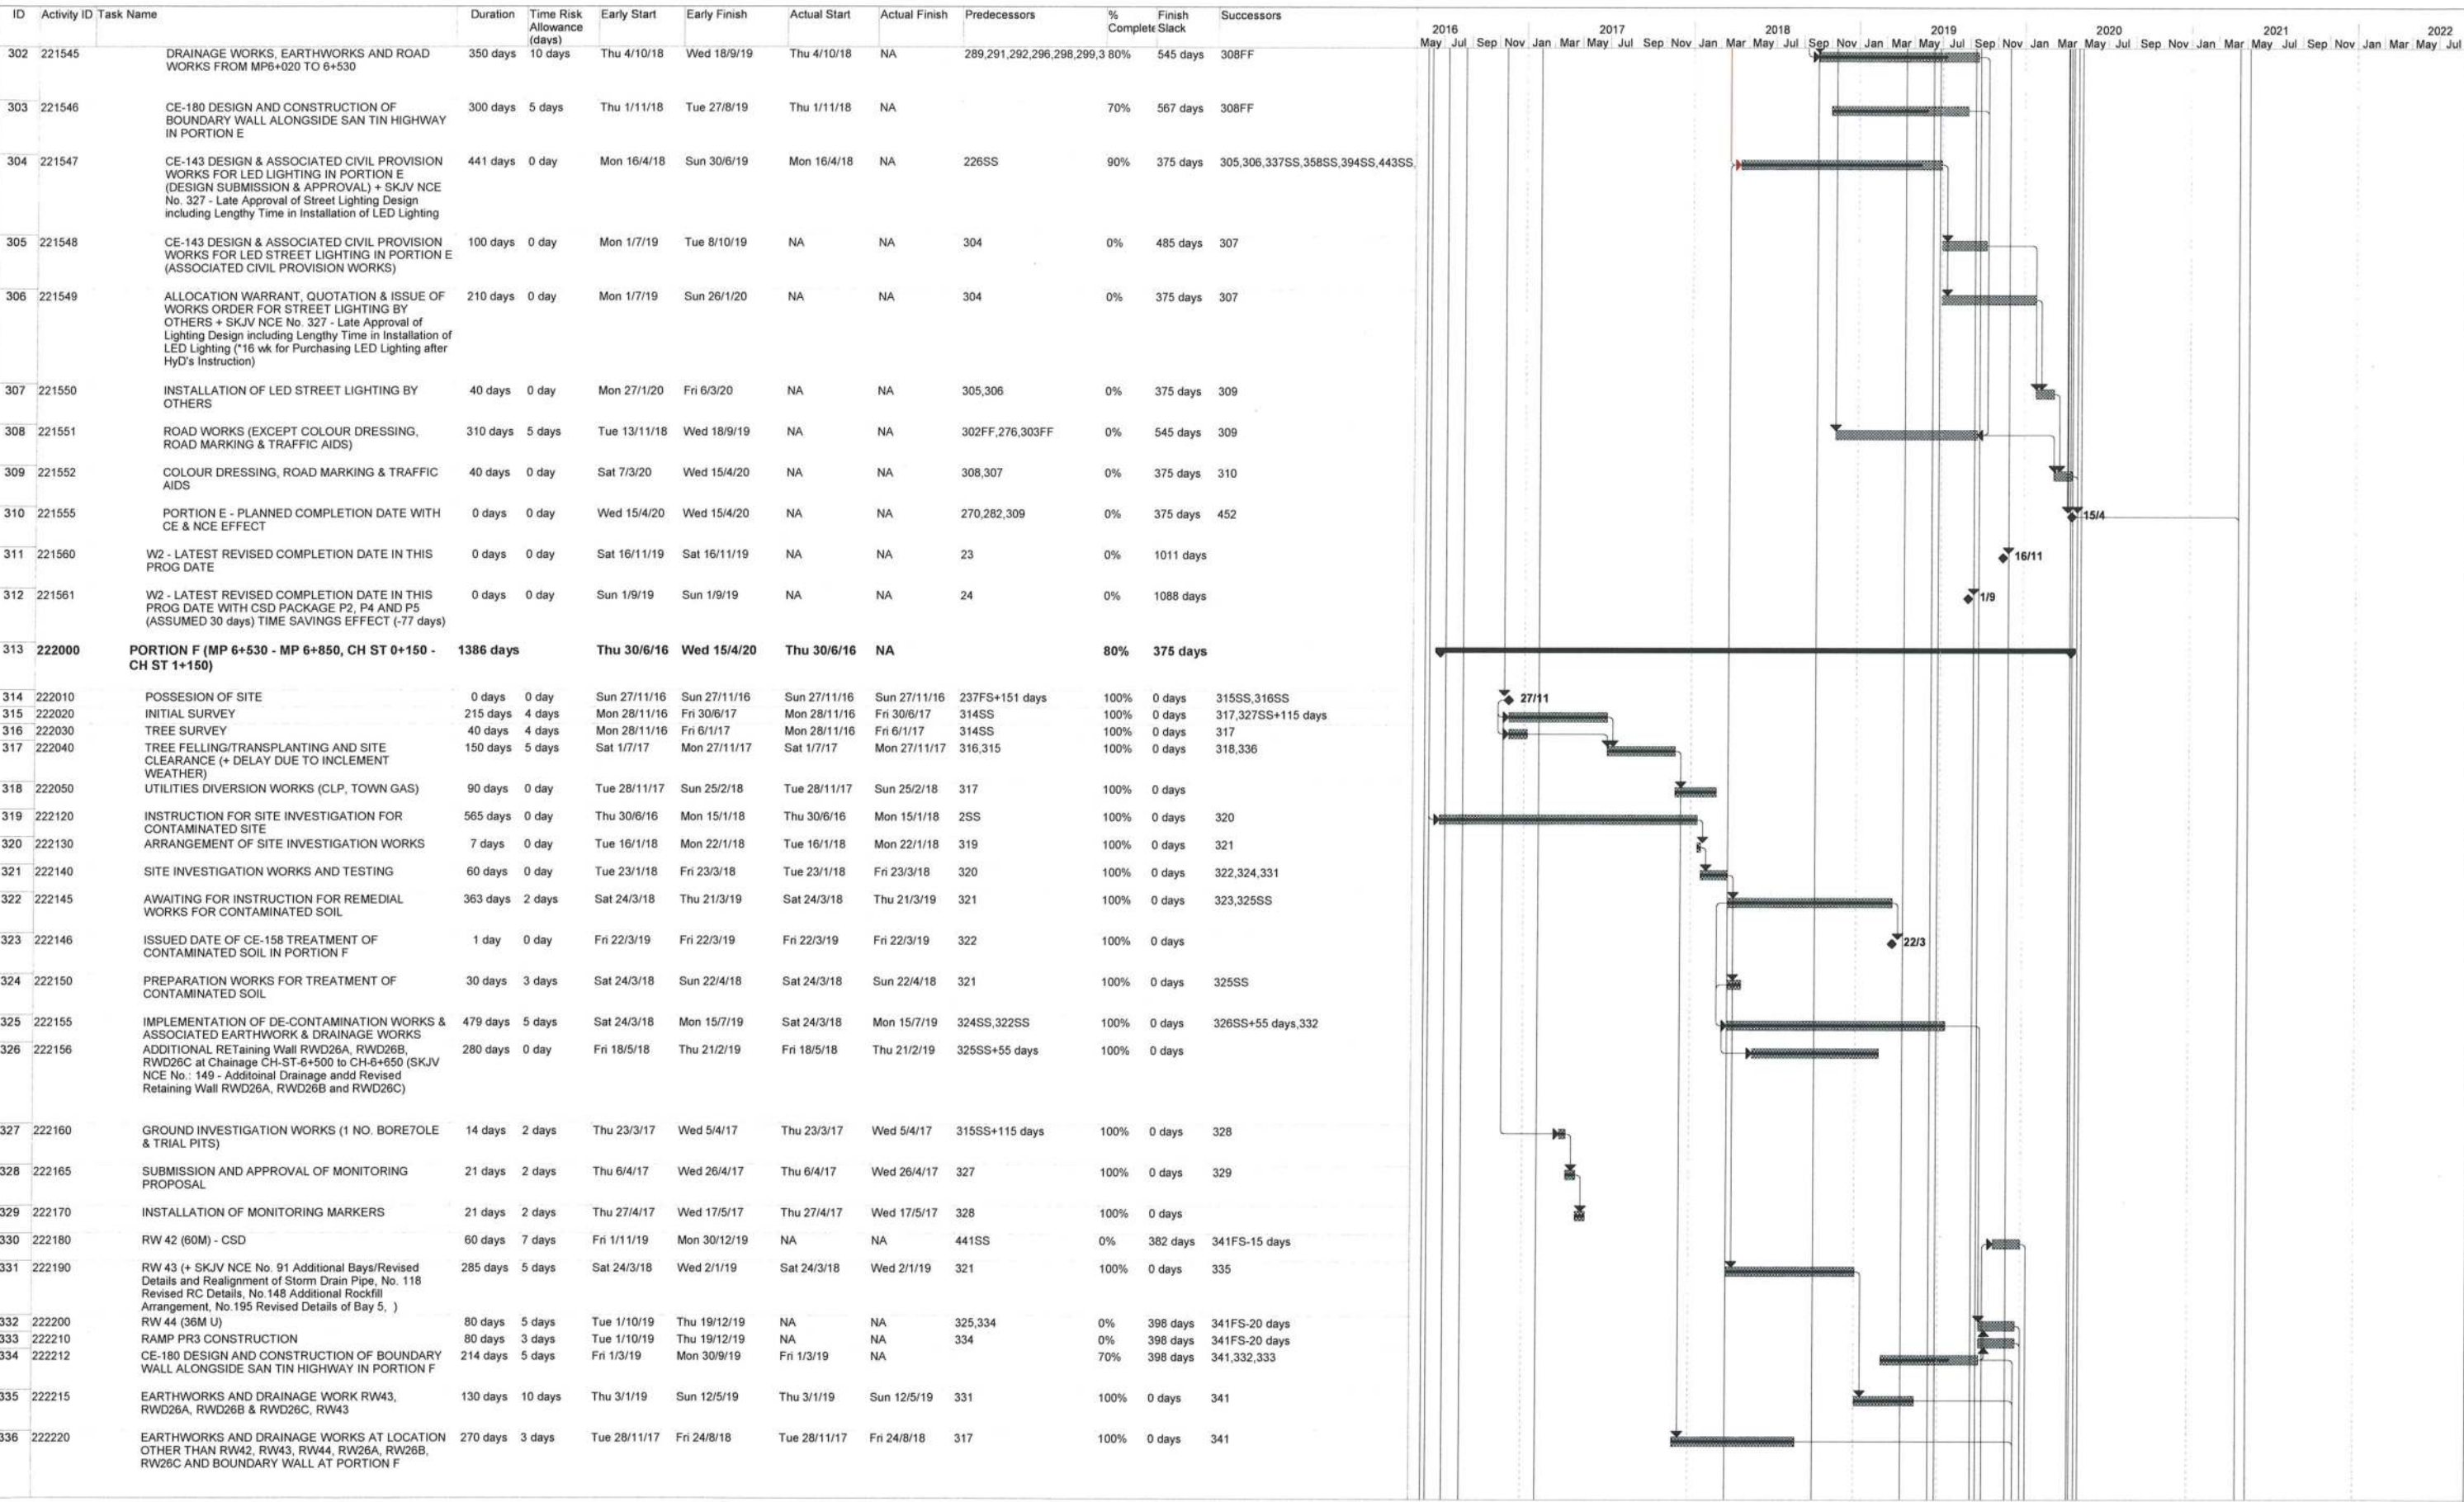


Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Progress		Deadline		Critical		Critical Split
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Critical		Deadline		Critical Split		Critical		Critical Split
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Critical		Deadline		Critical Split		Critical		Critical Split


8

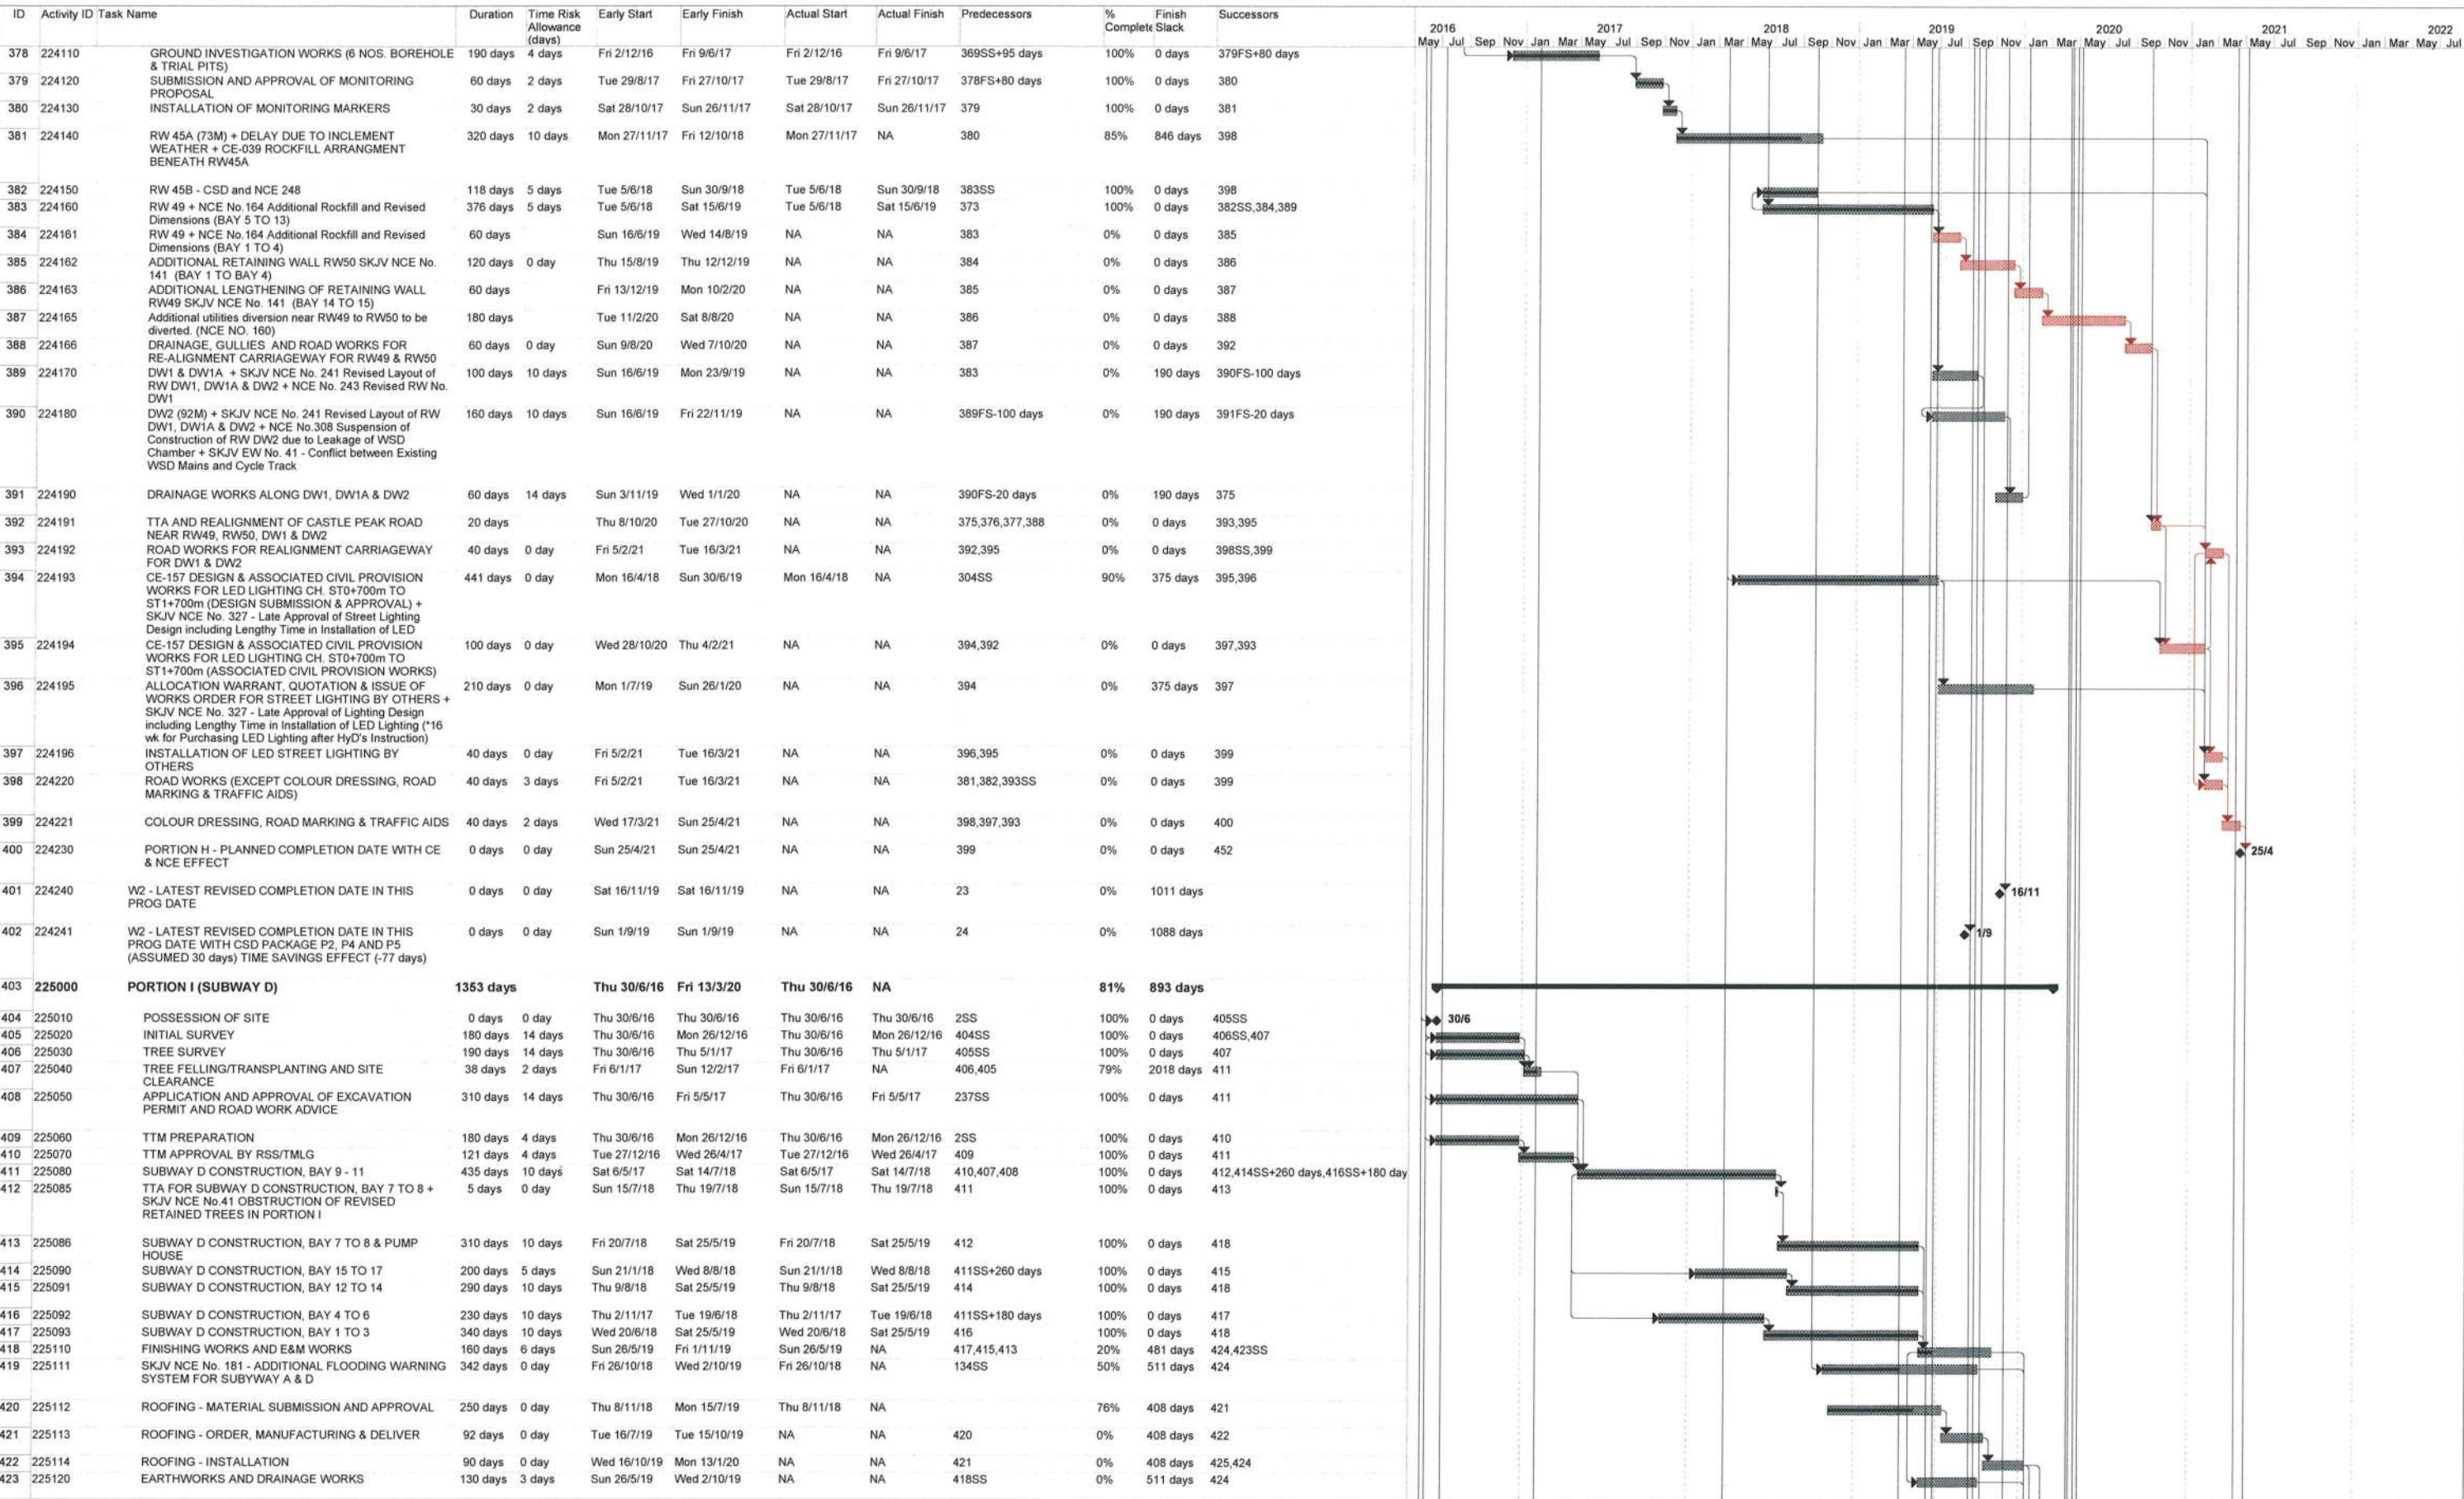


REMARK: ALL SUNDAYS AND HOLIDAYS ARE INCLUDED IN THIS PROGRAMME

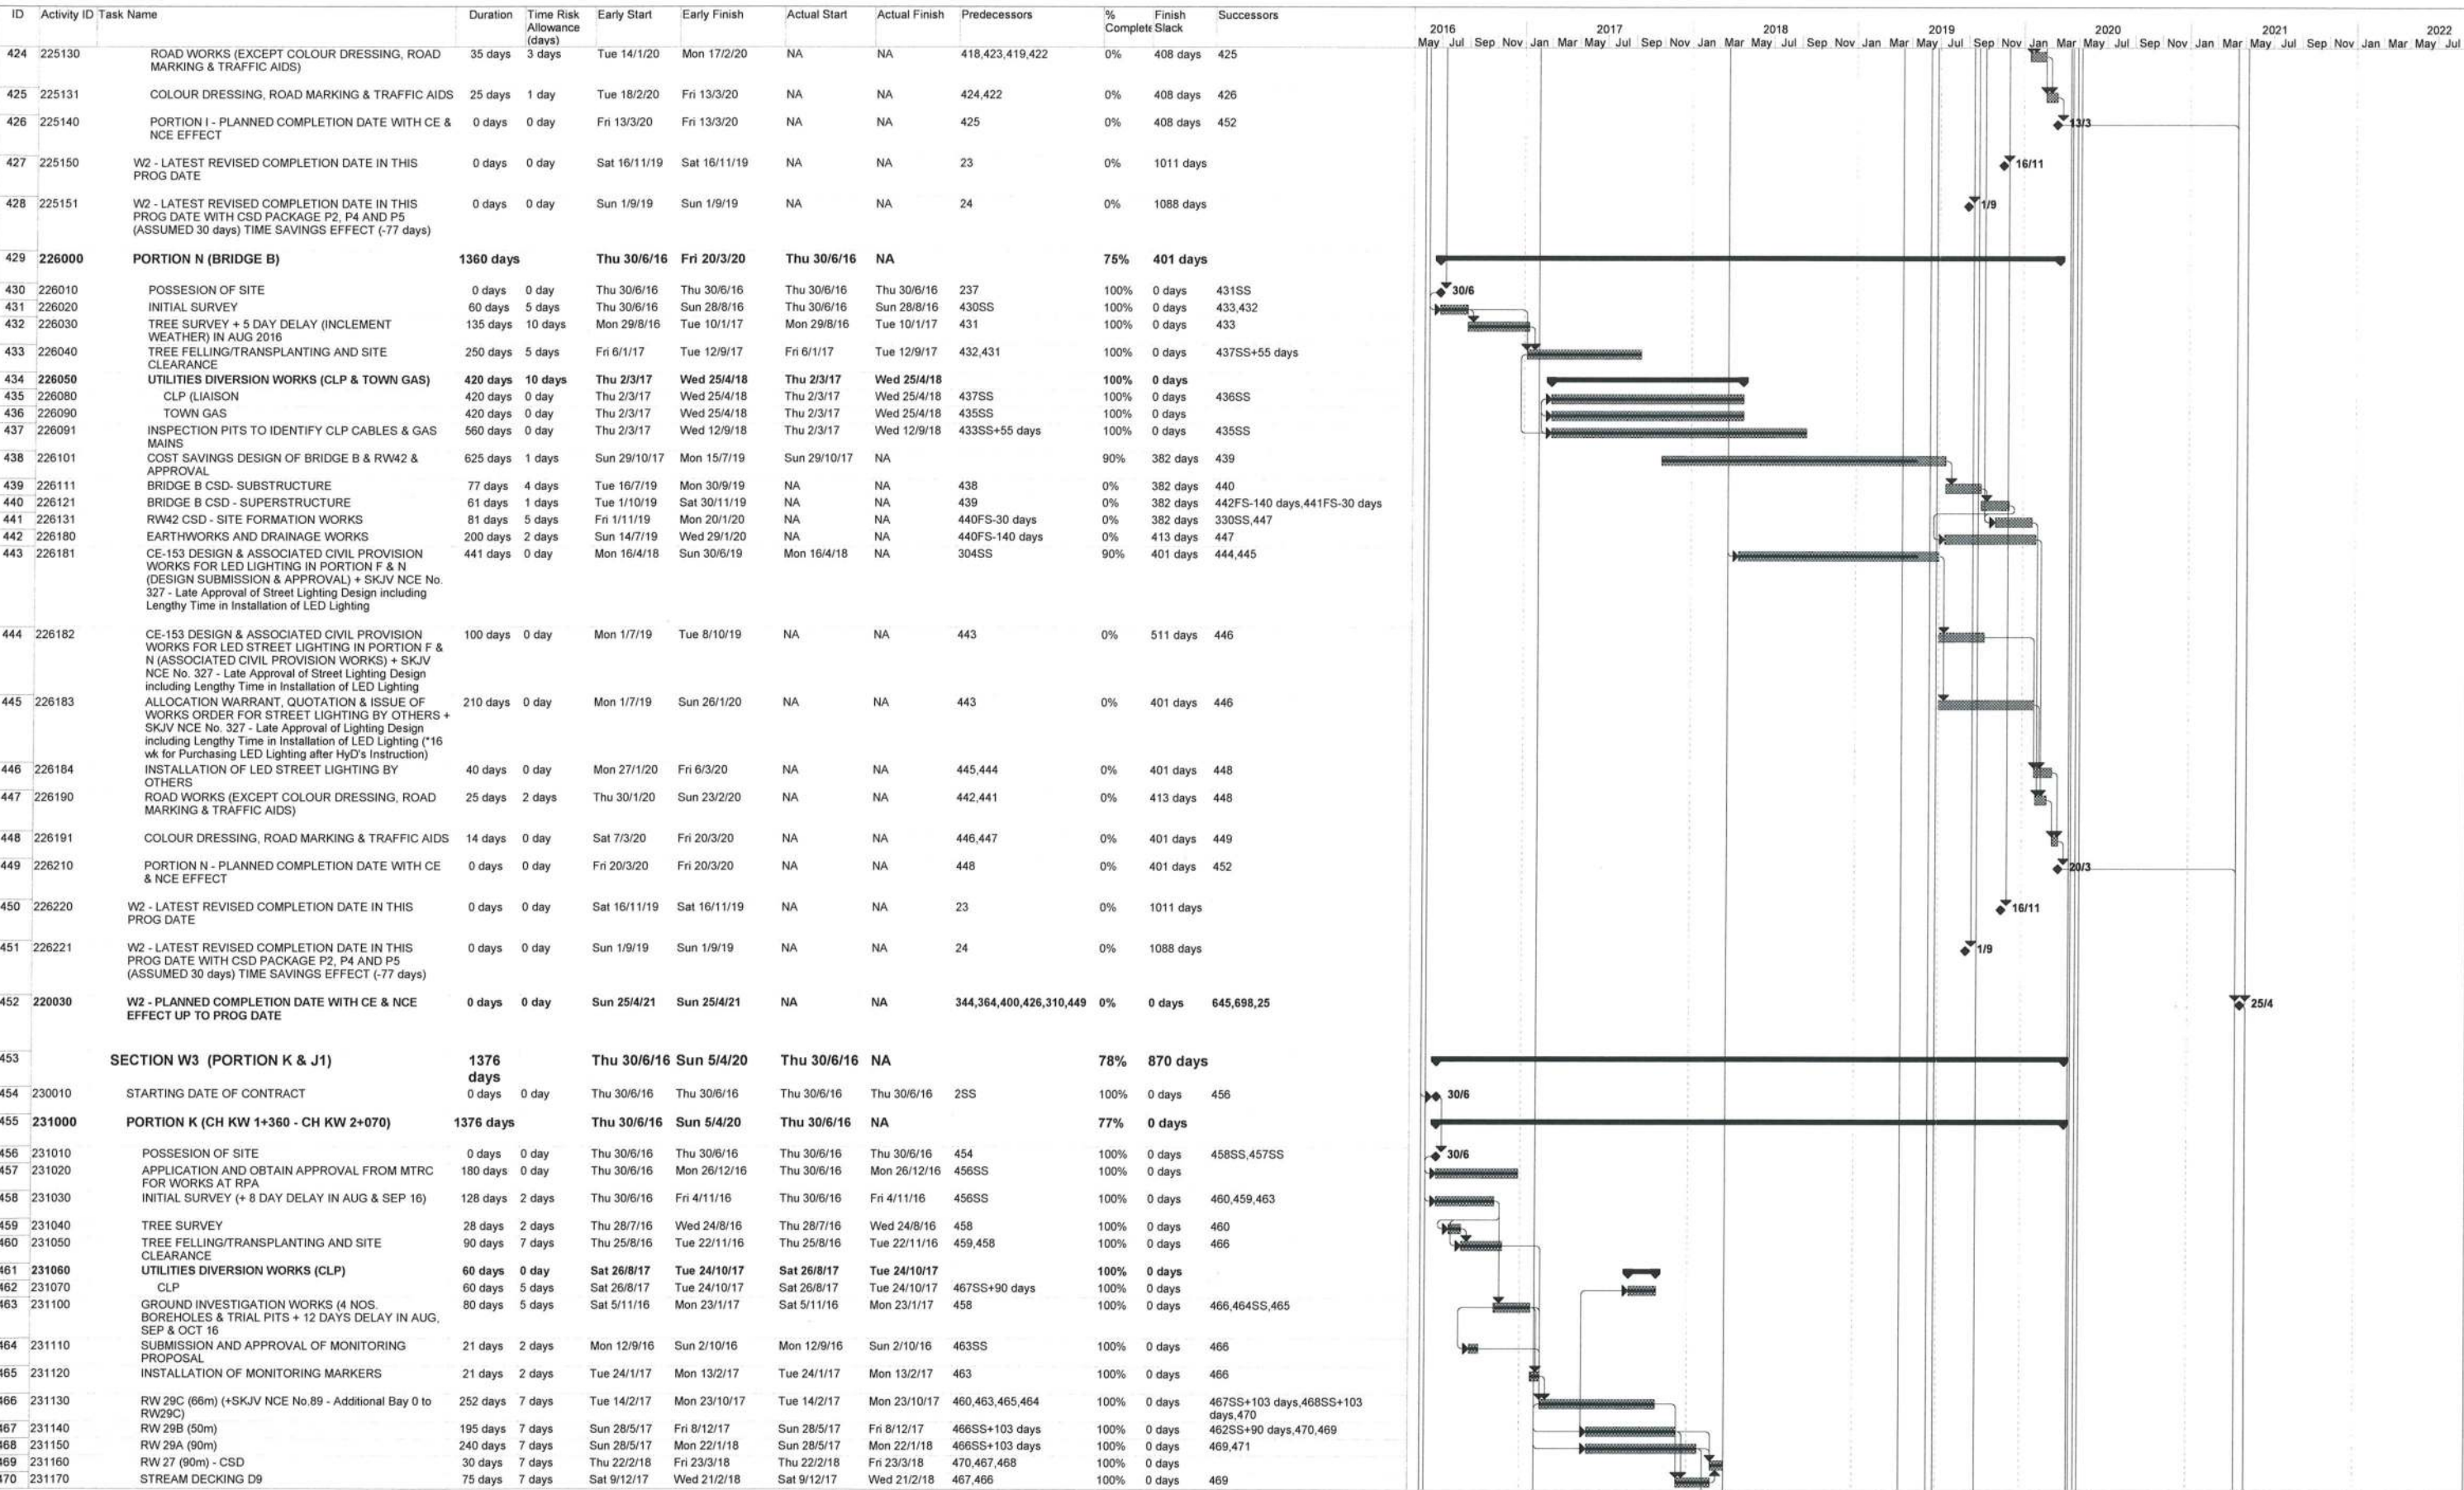

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Progress		Deadline
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Critical		Critical Split		
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Critical Split				

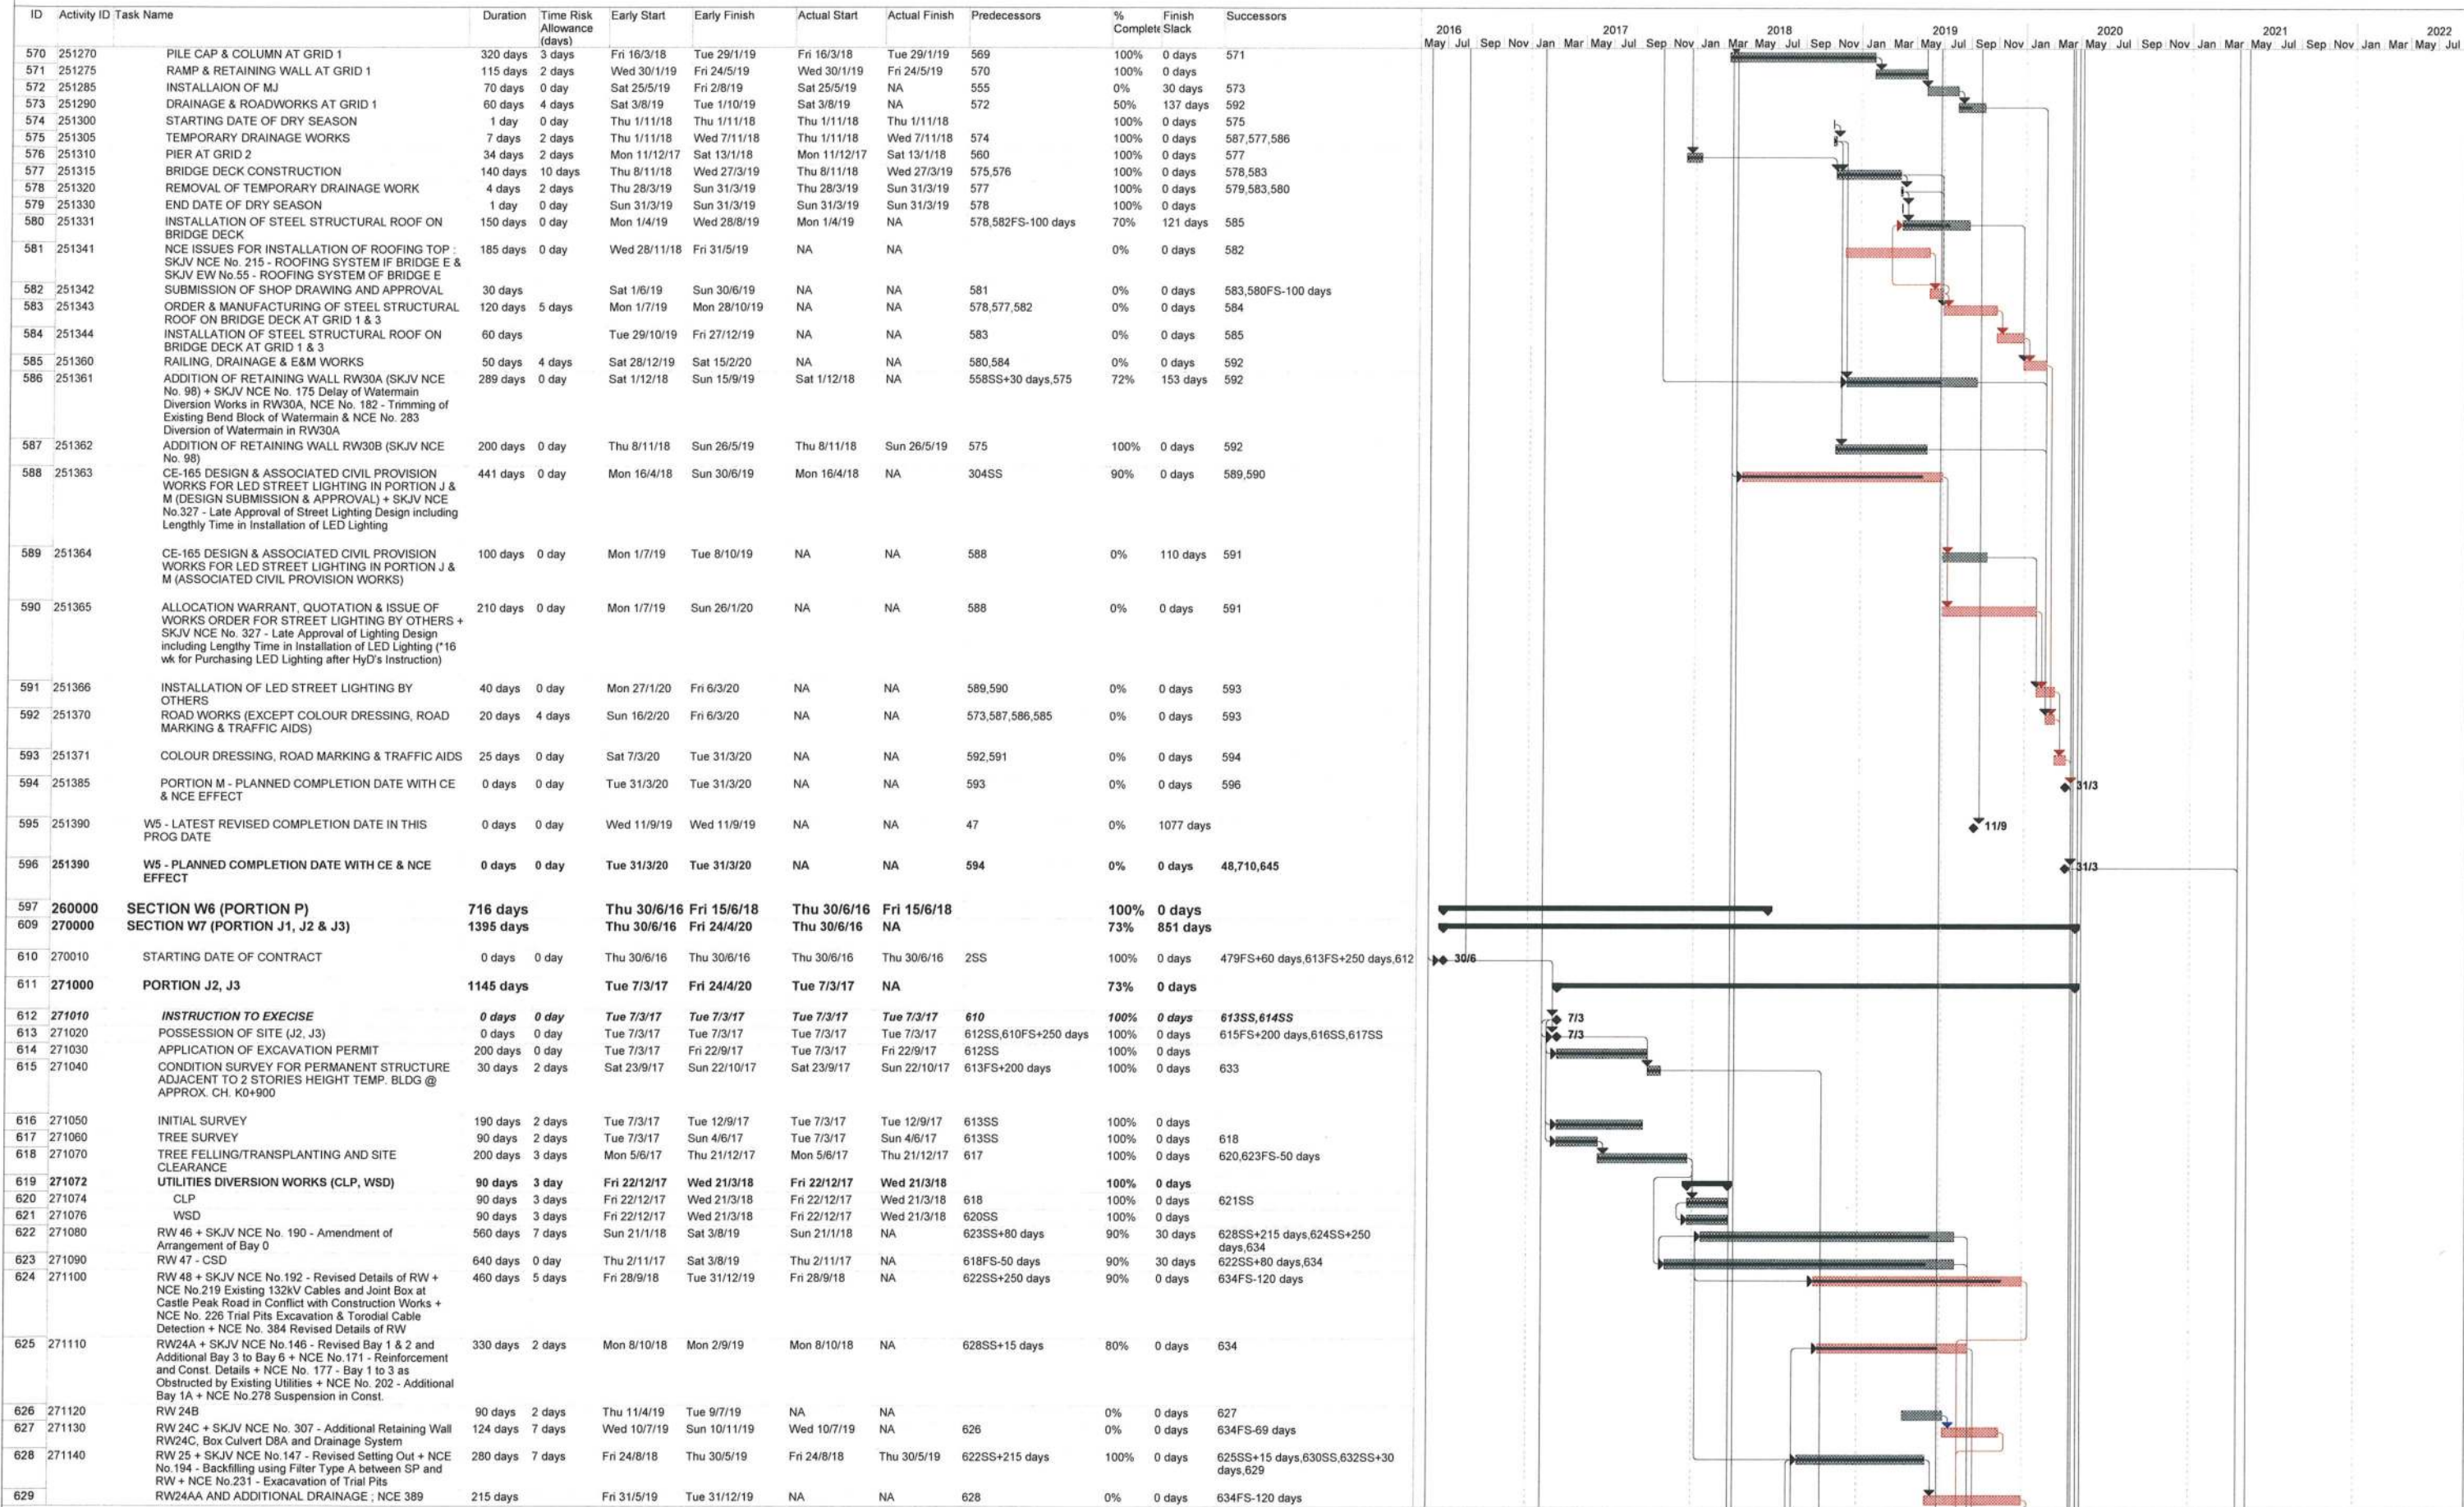


REMARK: ALL SUNDAYS AND HOLIDAYS ARE INCLUDED IN THIS PROGRAMME

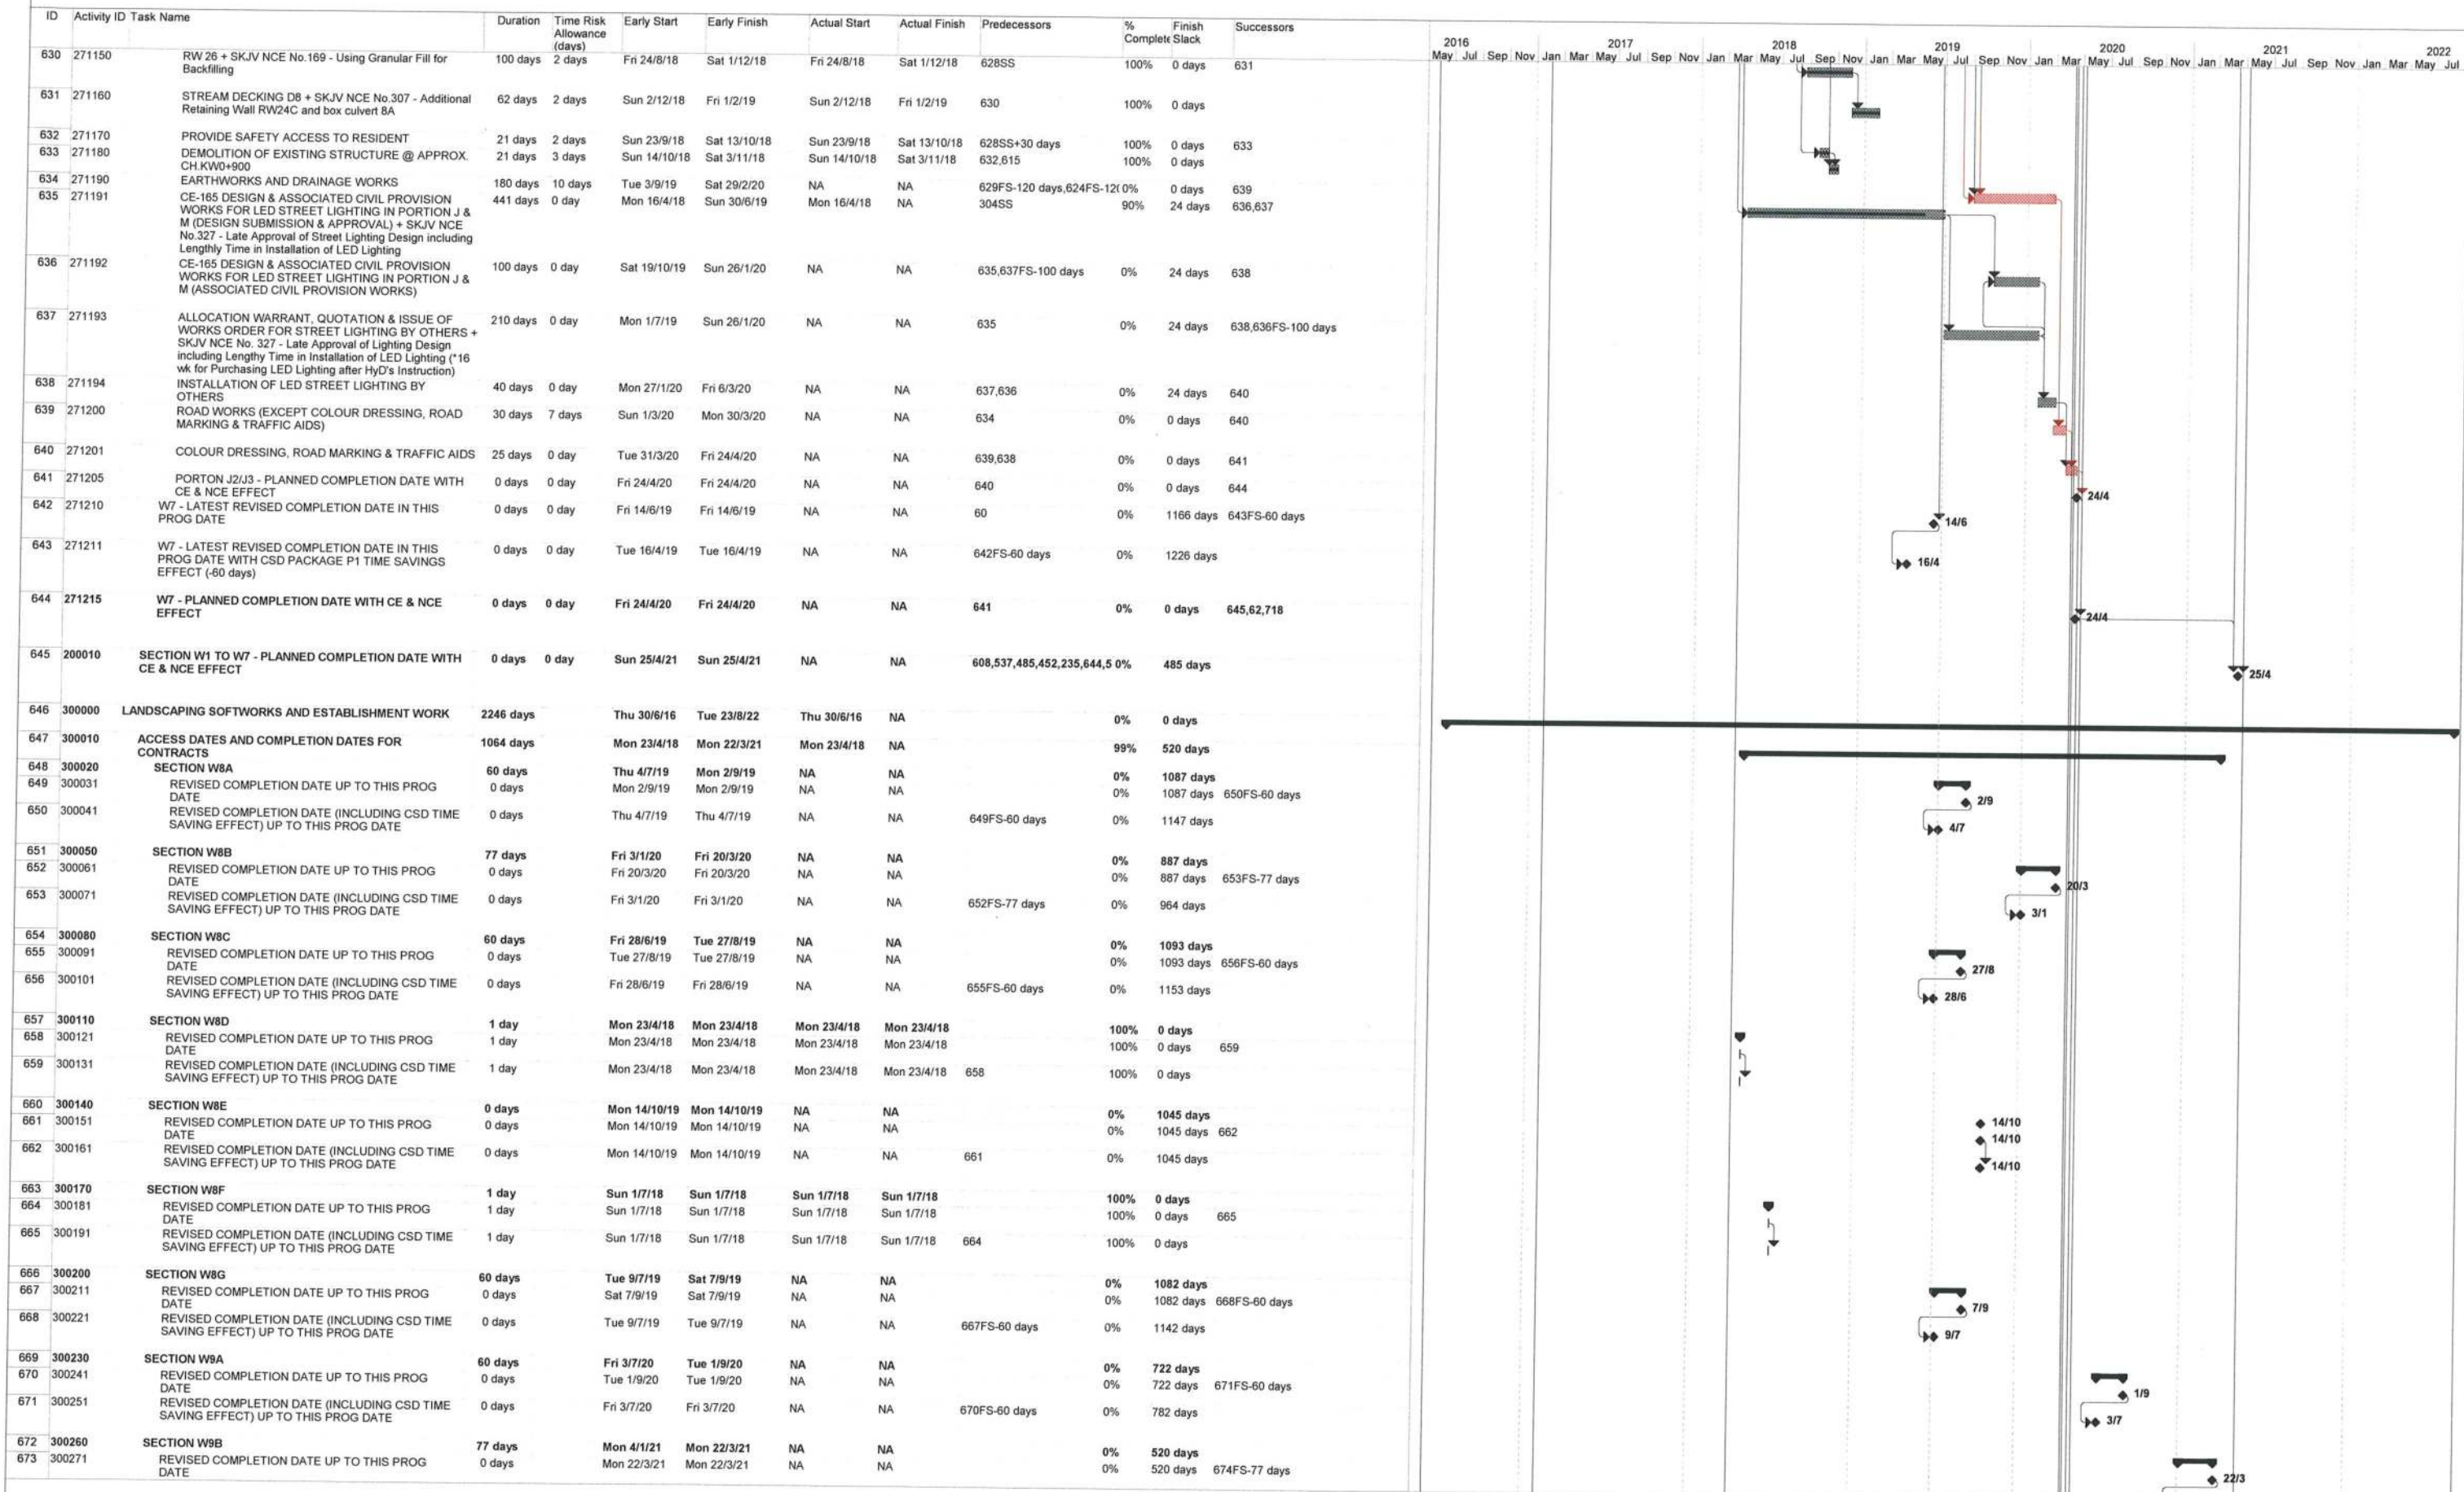

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only	Progress
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Critical	Deadline
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Critical Split	

REMARK: ALL SUNDAYS AND HOLIDAYS ARE INCLUDED IN THIS PROGRAMME

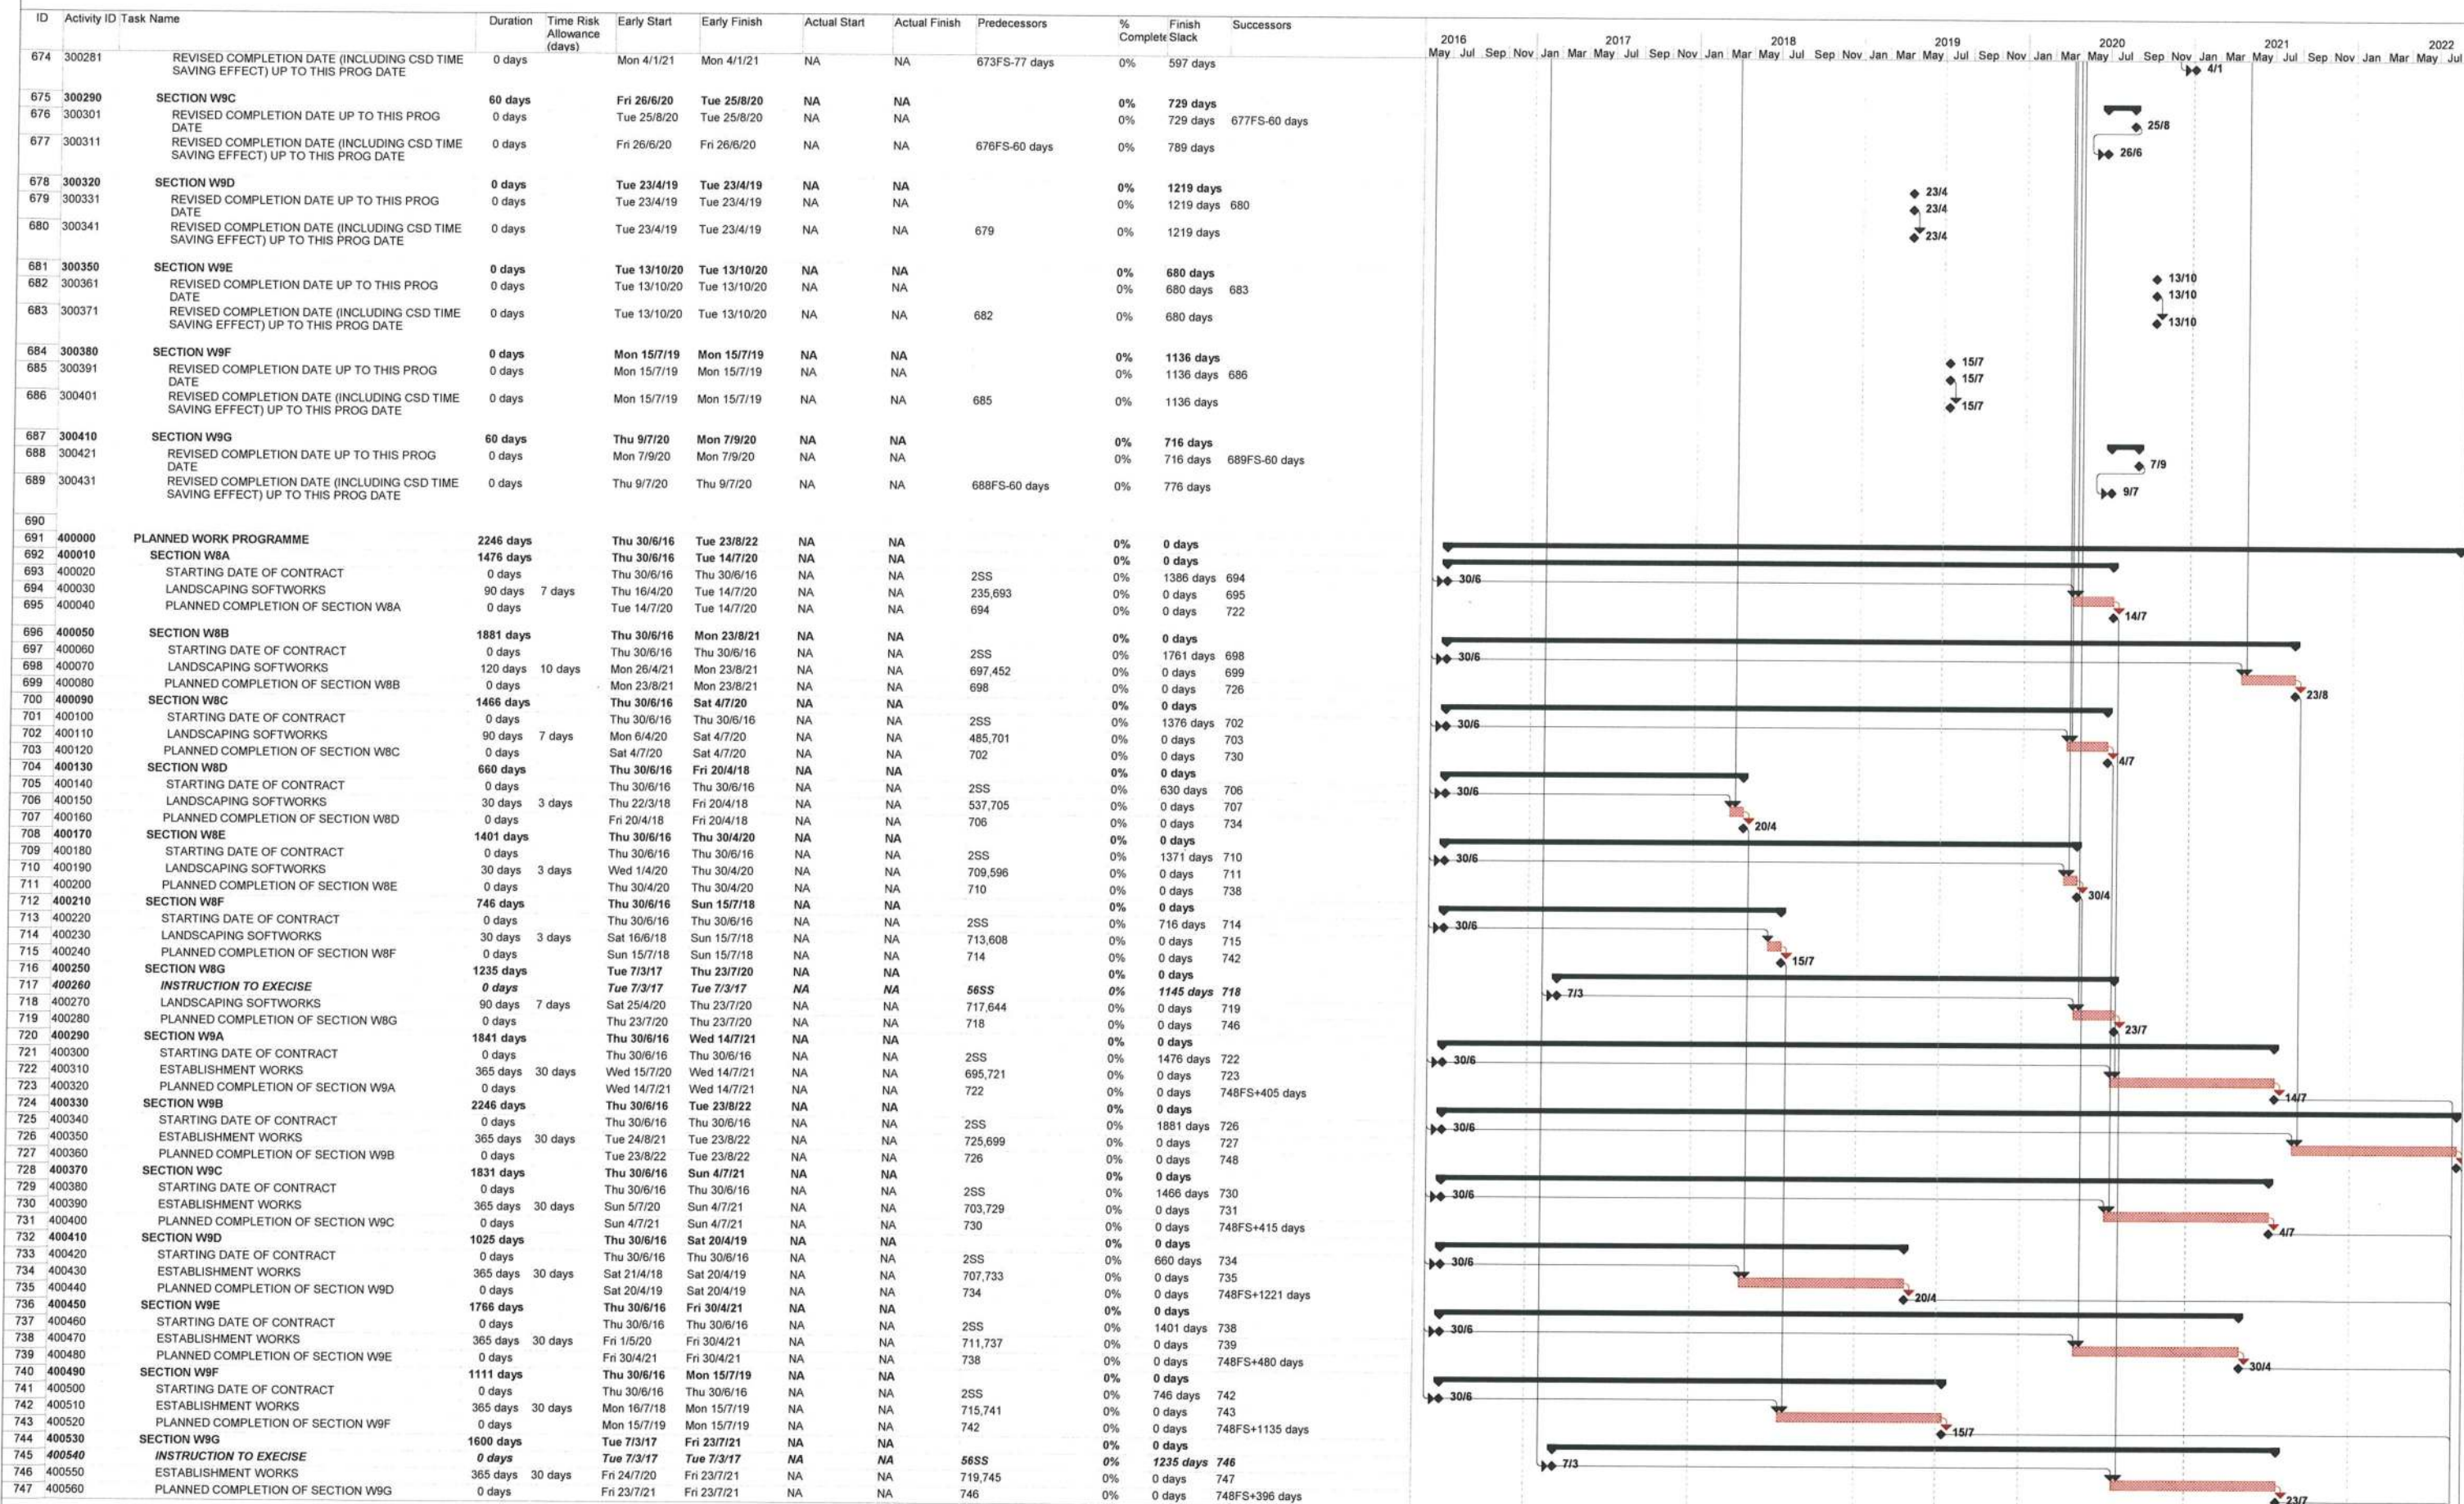

ID	Activity ID	Task Name	Duration	Time Risk Allowance (days)	Early Start	Early Finish	Actual Start	Actual Finish	Predecessors	% Complete	Finish Slack	Successors	2016				2017				2018				2019				2020				2021				2022			
748	400560	PLANNED COMPLETION OF OVERALL ESTABLISHMENT WORKS	0 days		Tue 23/8/22	Tue 23/8/22	NA	NA	727,735FS+1221 days,731FS+415	0%	0 days		May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul		

Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only		Progress	
Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Critical		Deadline	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Critical Split			
