


**Maeda Corporation**  
 Contract No. DC/2005/01  
 Expansion of Shek Wu Hui Sewage Treatment Works and  
 Upgrading of Ting Kok Road Pumping Station No.5  
**Master Programme (Rev. 2)**



Date: Fri 06/7/28


Task		Progress		Summary		Rolled Up Critical Task		Rolled Up Progress		External Tasks	
Critical Task		Milestone		Rolled Up Task		Rolled Up Milestone		Split		Project Summary	

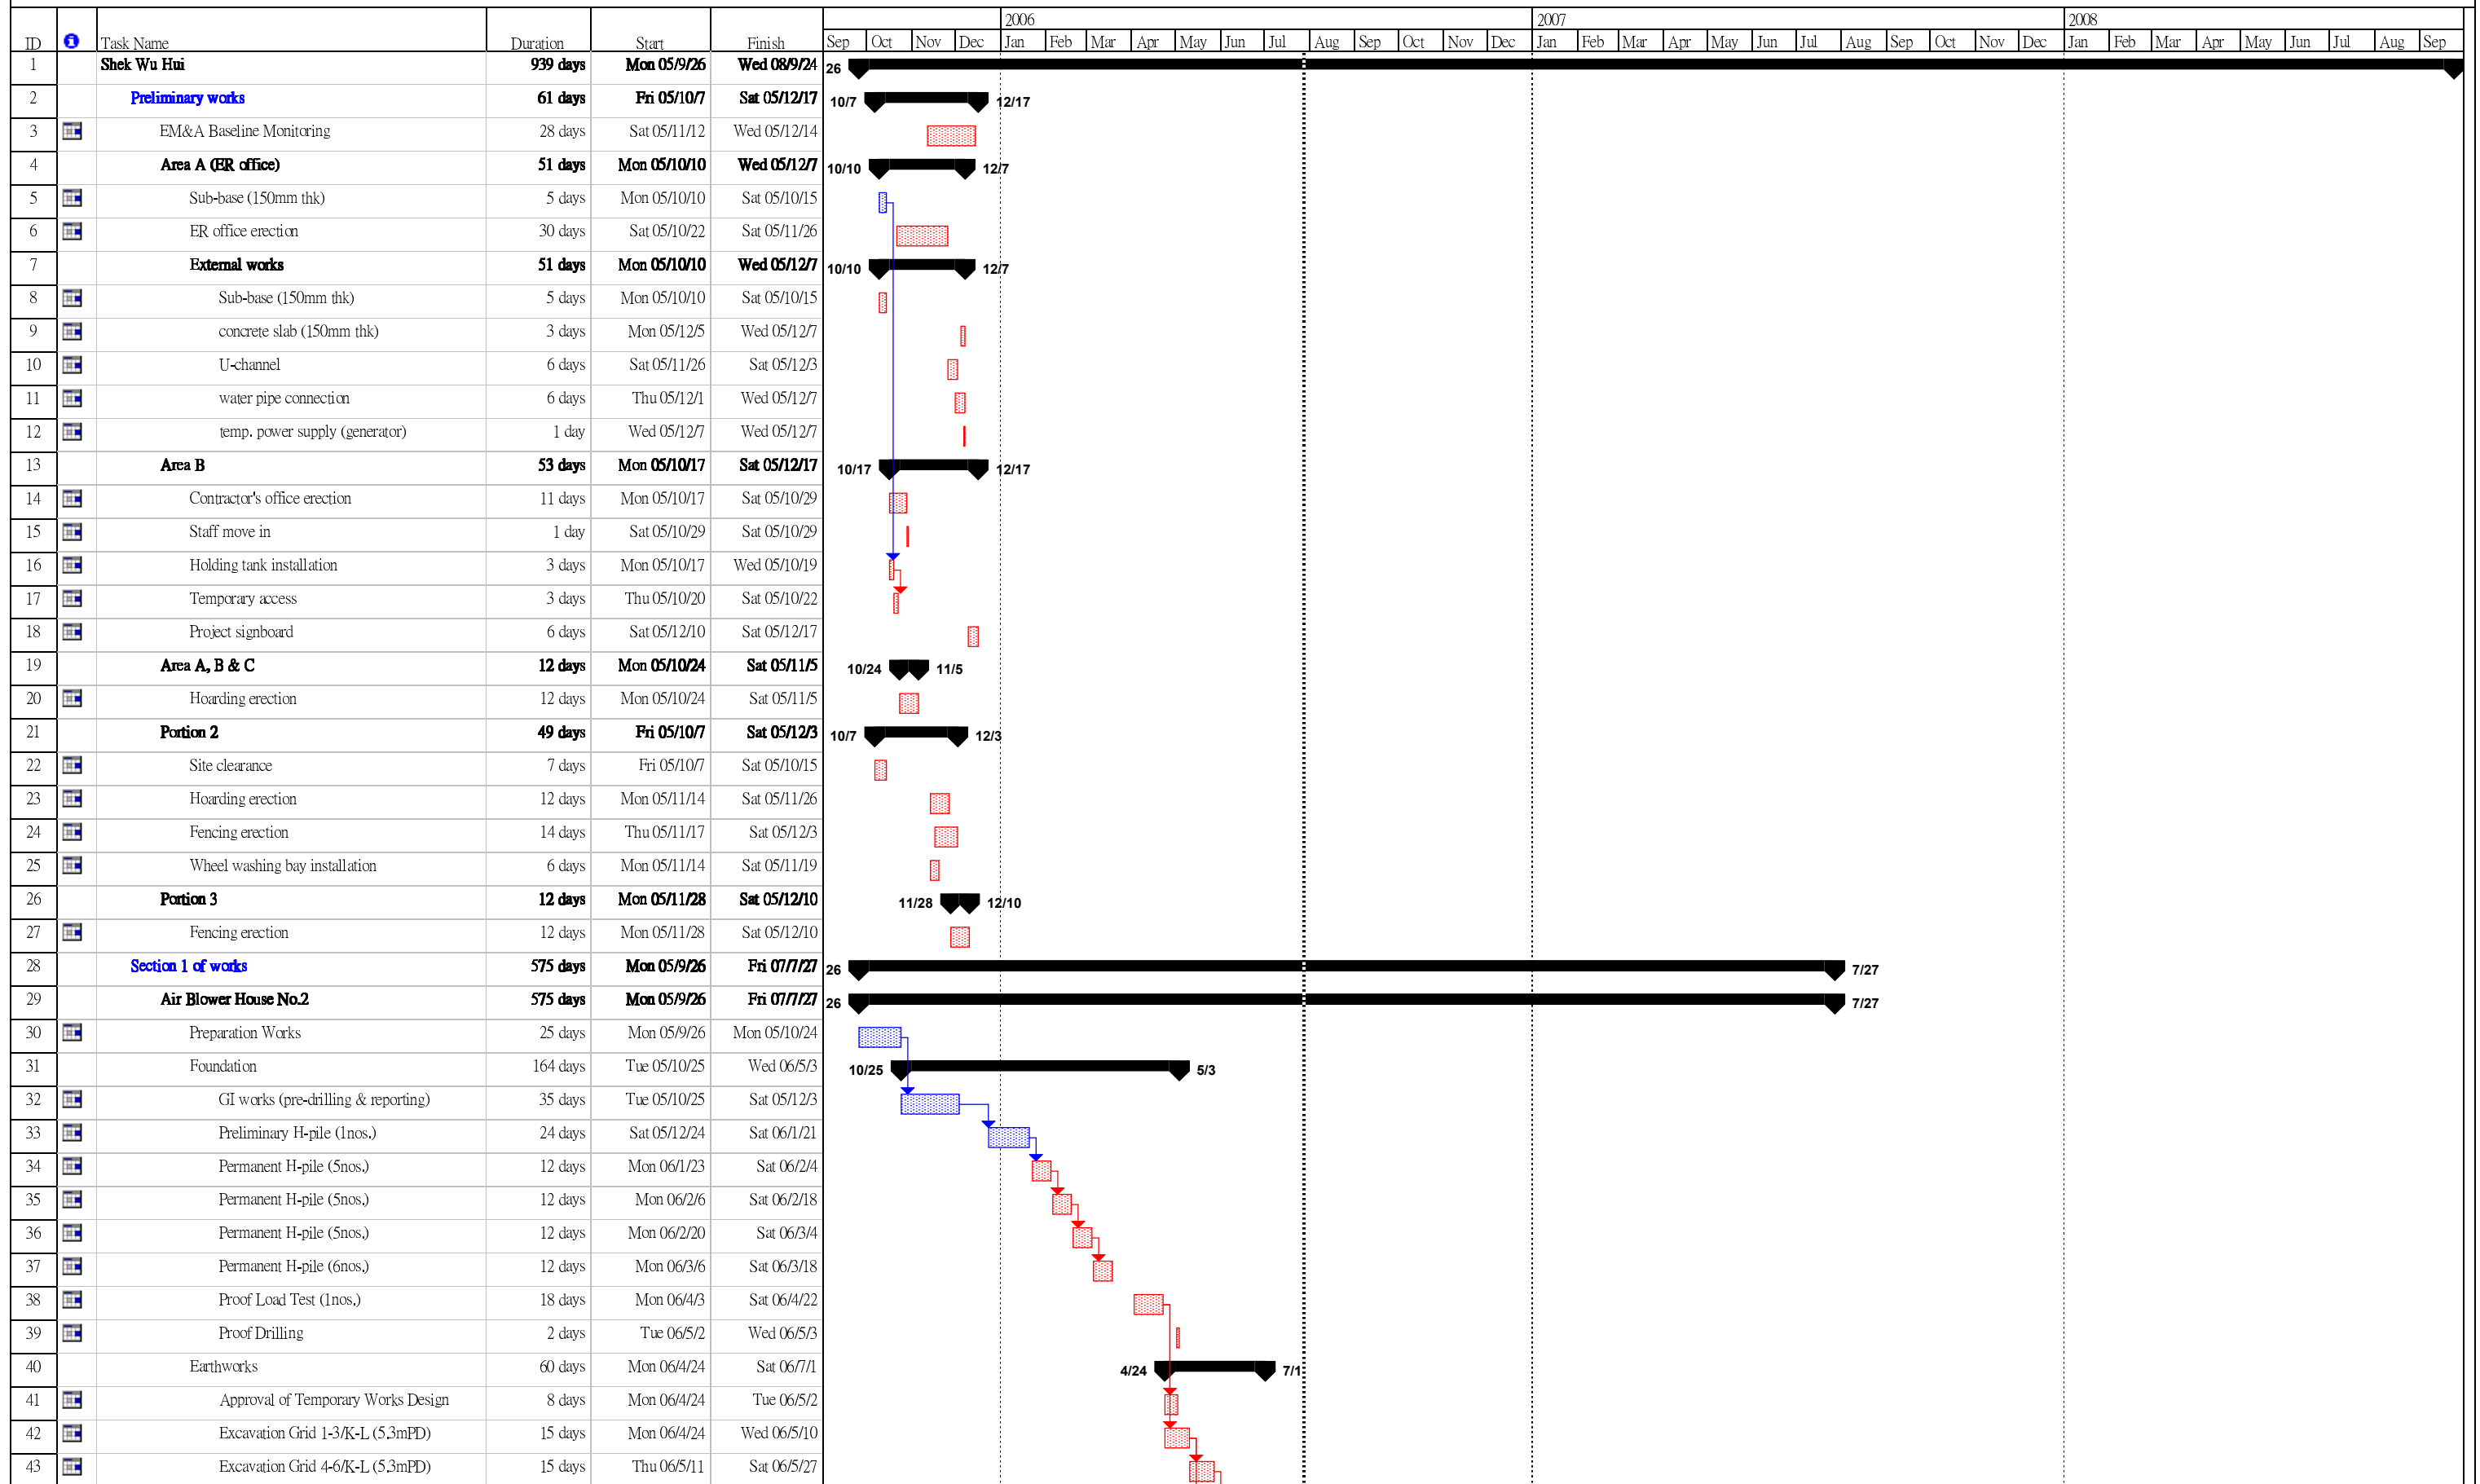





**Maeda Corporation**  
 Contract No. DC/2005/01  
 Expansion of Shek Wu Hui Sewage Treatment Works and  
 Upgrading of Ting Kok Road Pumping Station No.5  
**Master Programme (Rev. 2)**

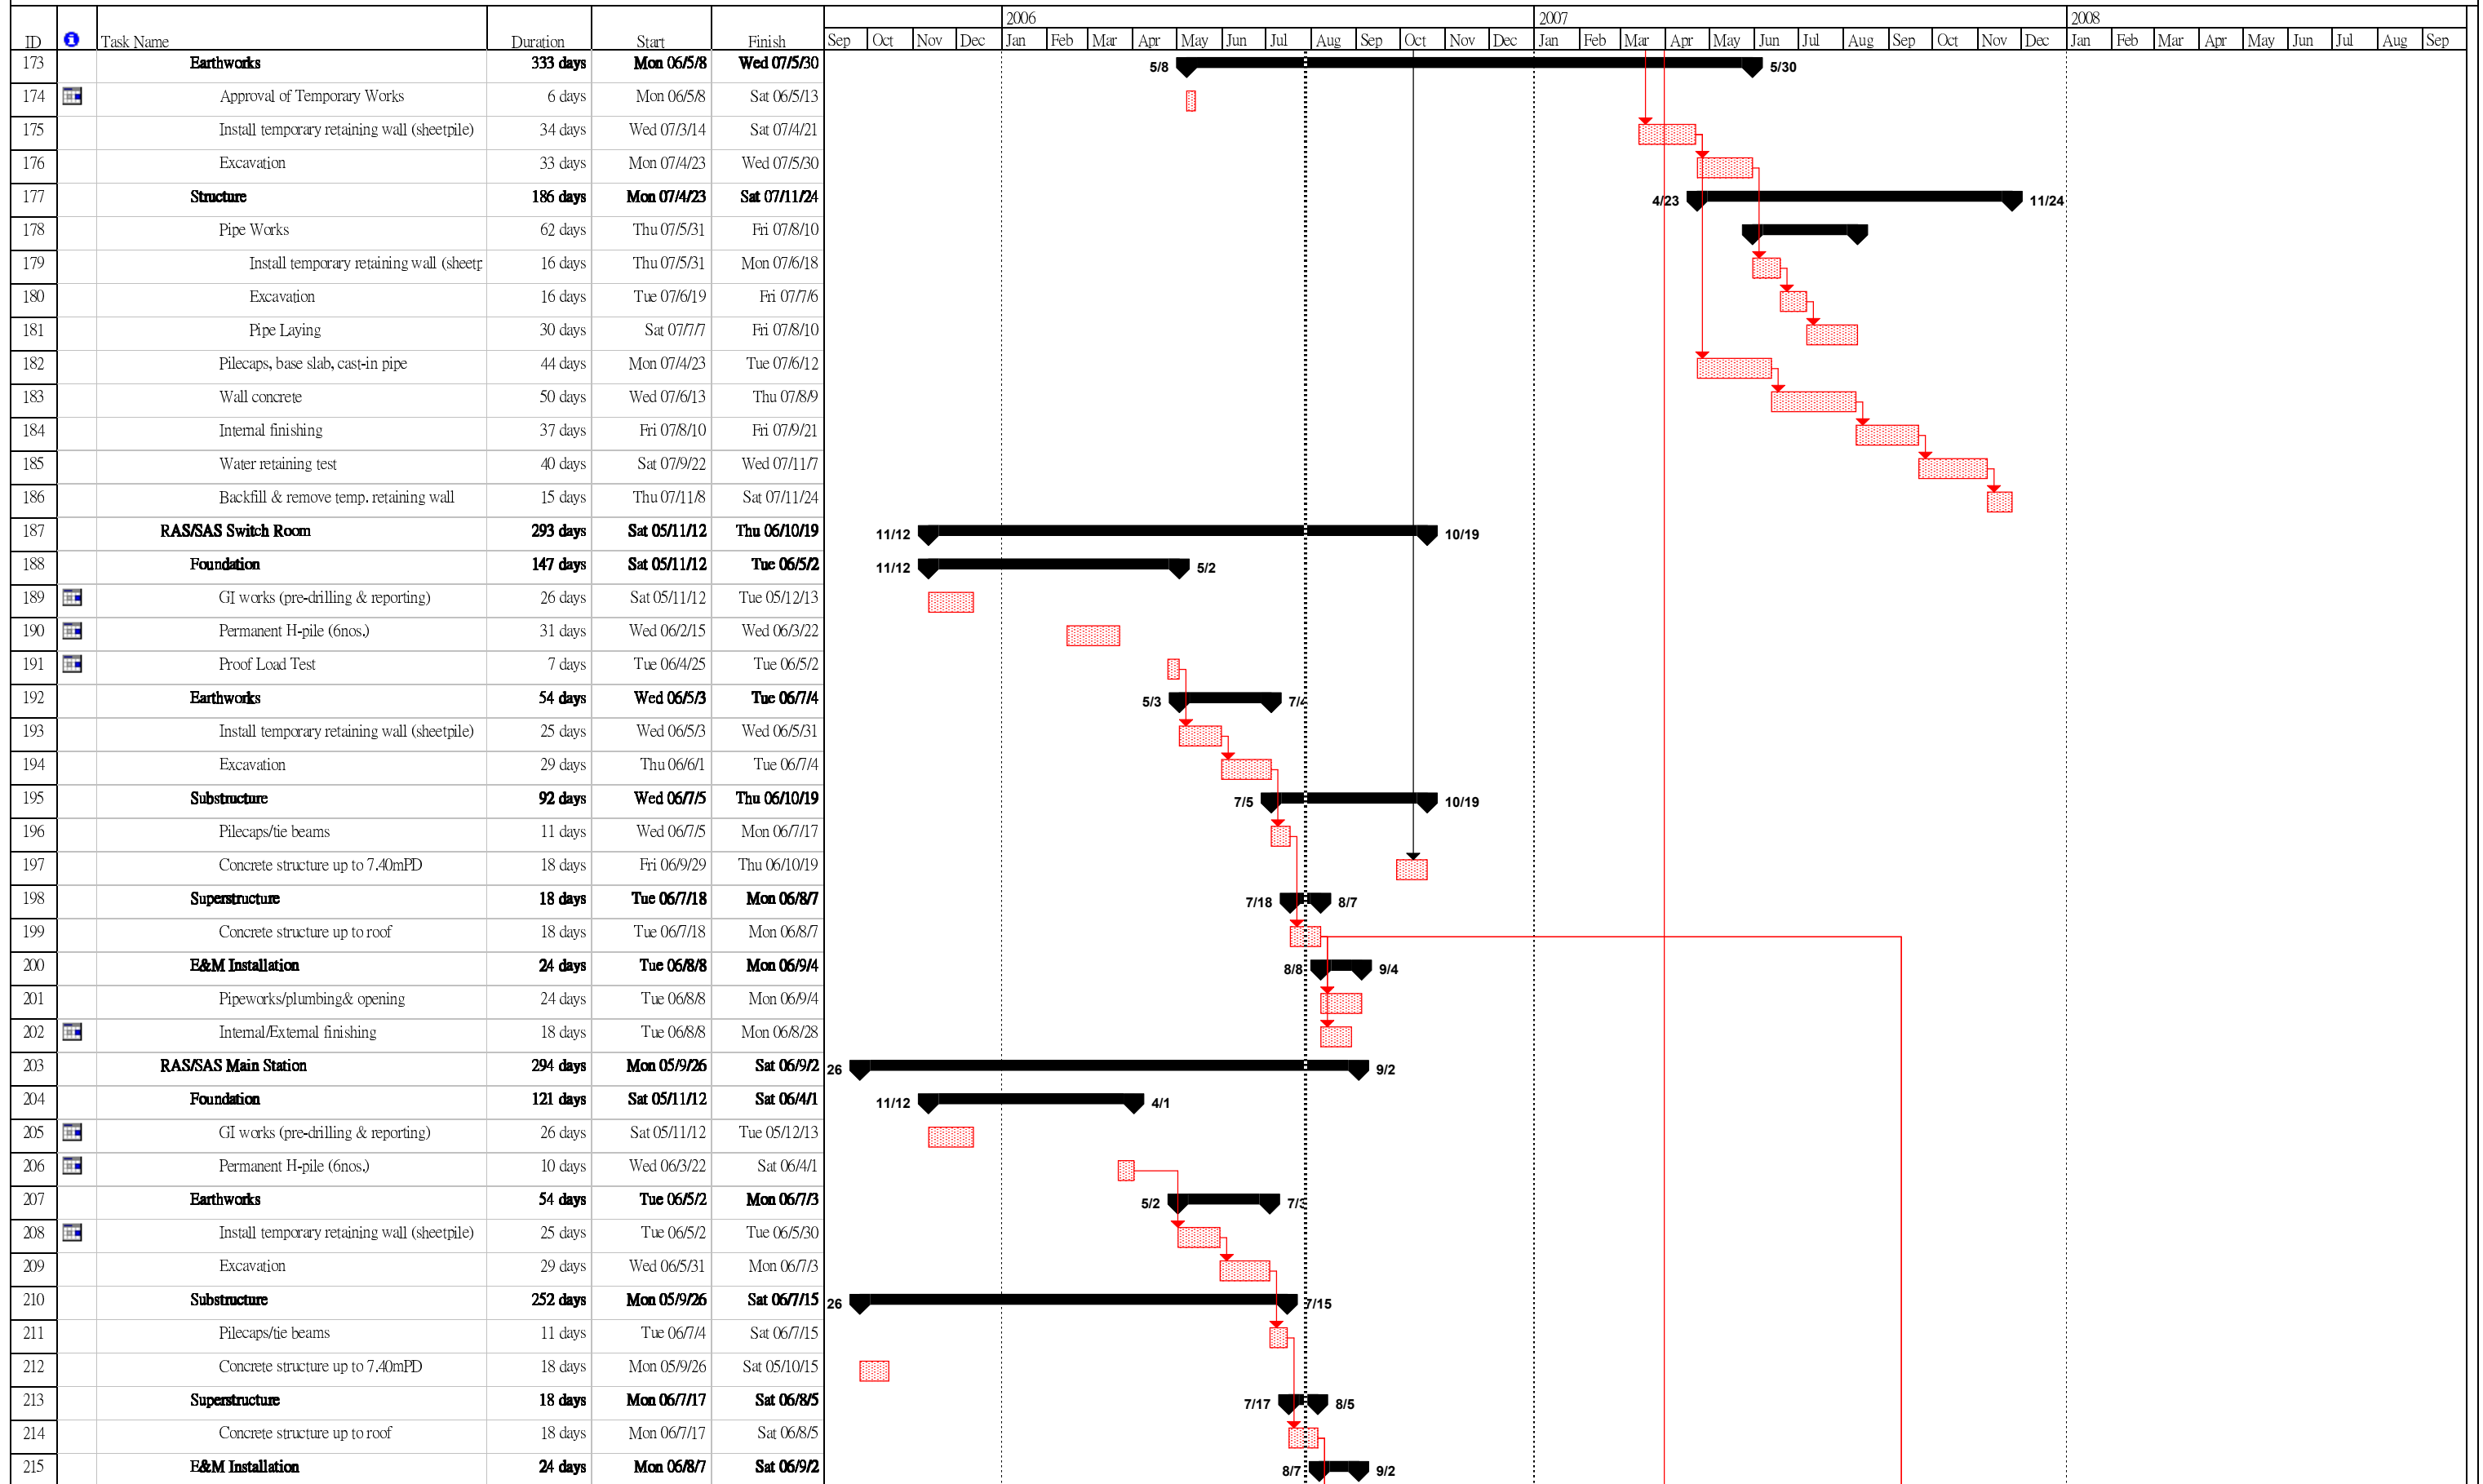


Date: Fri 06/7/28

Task		Progress		Summary		Rolled Up Critical Task		Rolled Up Progress		External Tasks	
Critical Task		Milestone		Rolled Up Task		Rolled Up Milestone		Split		Project Summary	





**Maeda Corporation**  
 Contract No. DC/2005/01  
 Expansion of Shek Wu Hui Sewage Treatment Works and  
 Upgrading of Ting Kok Road Pumping Station No.5  
**Master Programme (Rev. 2)**

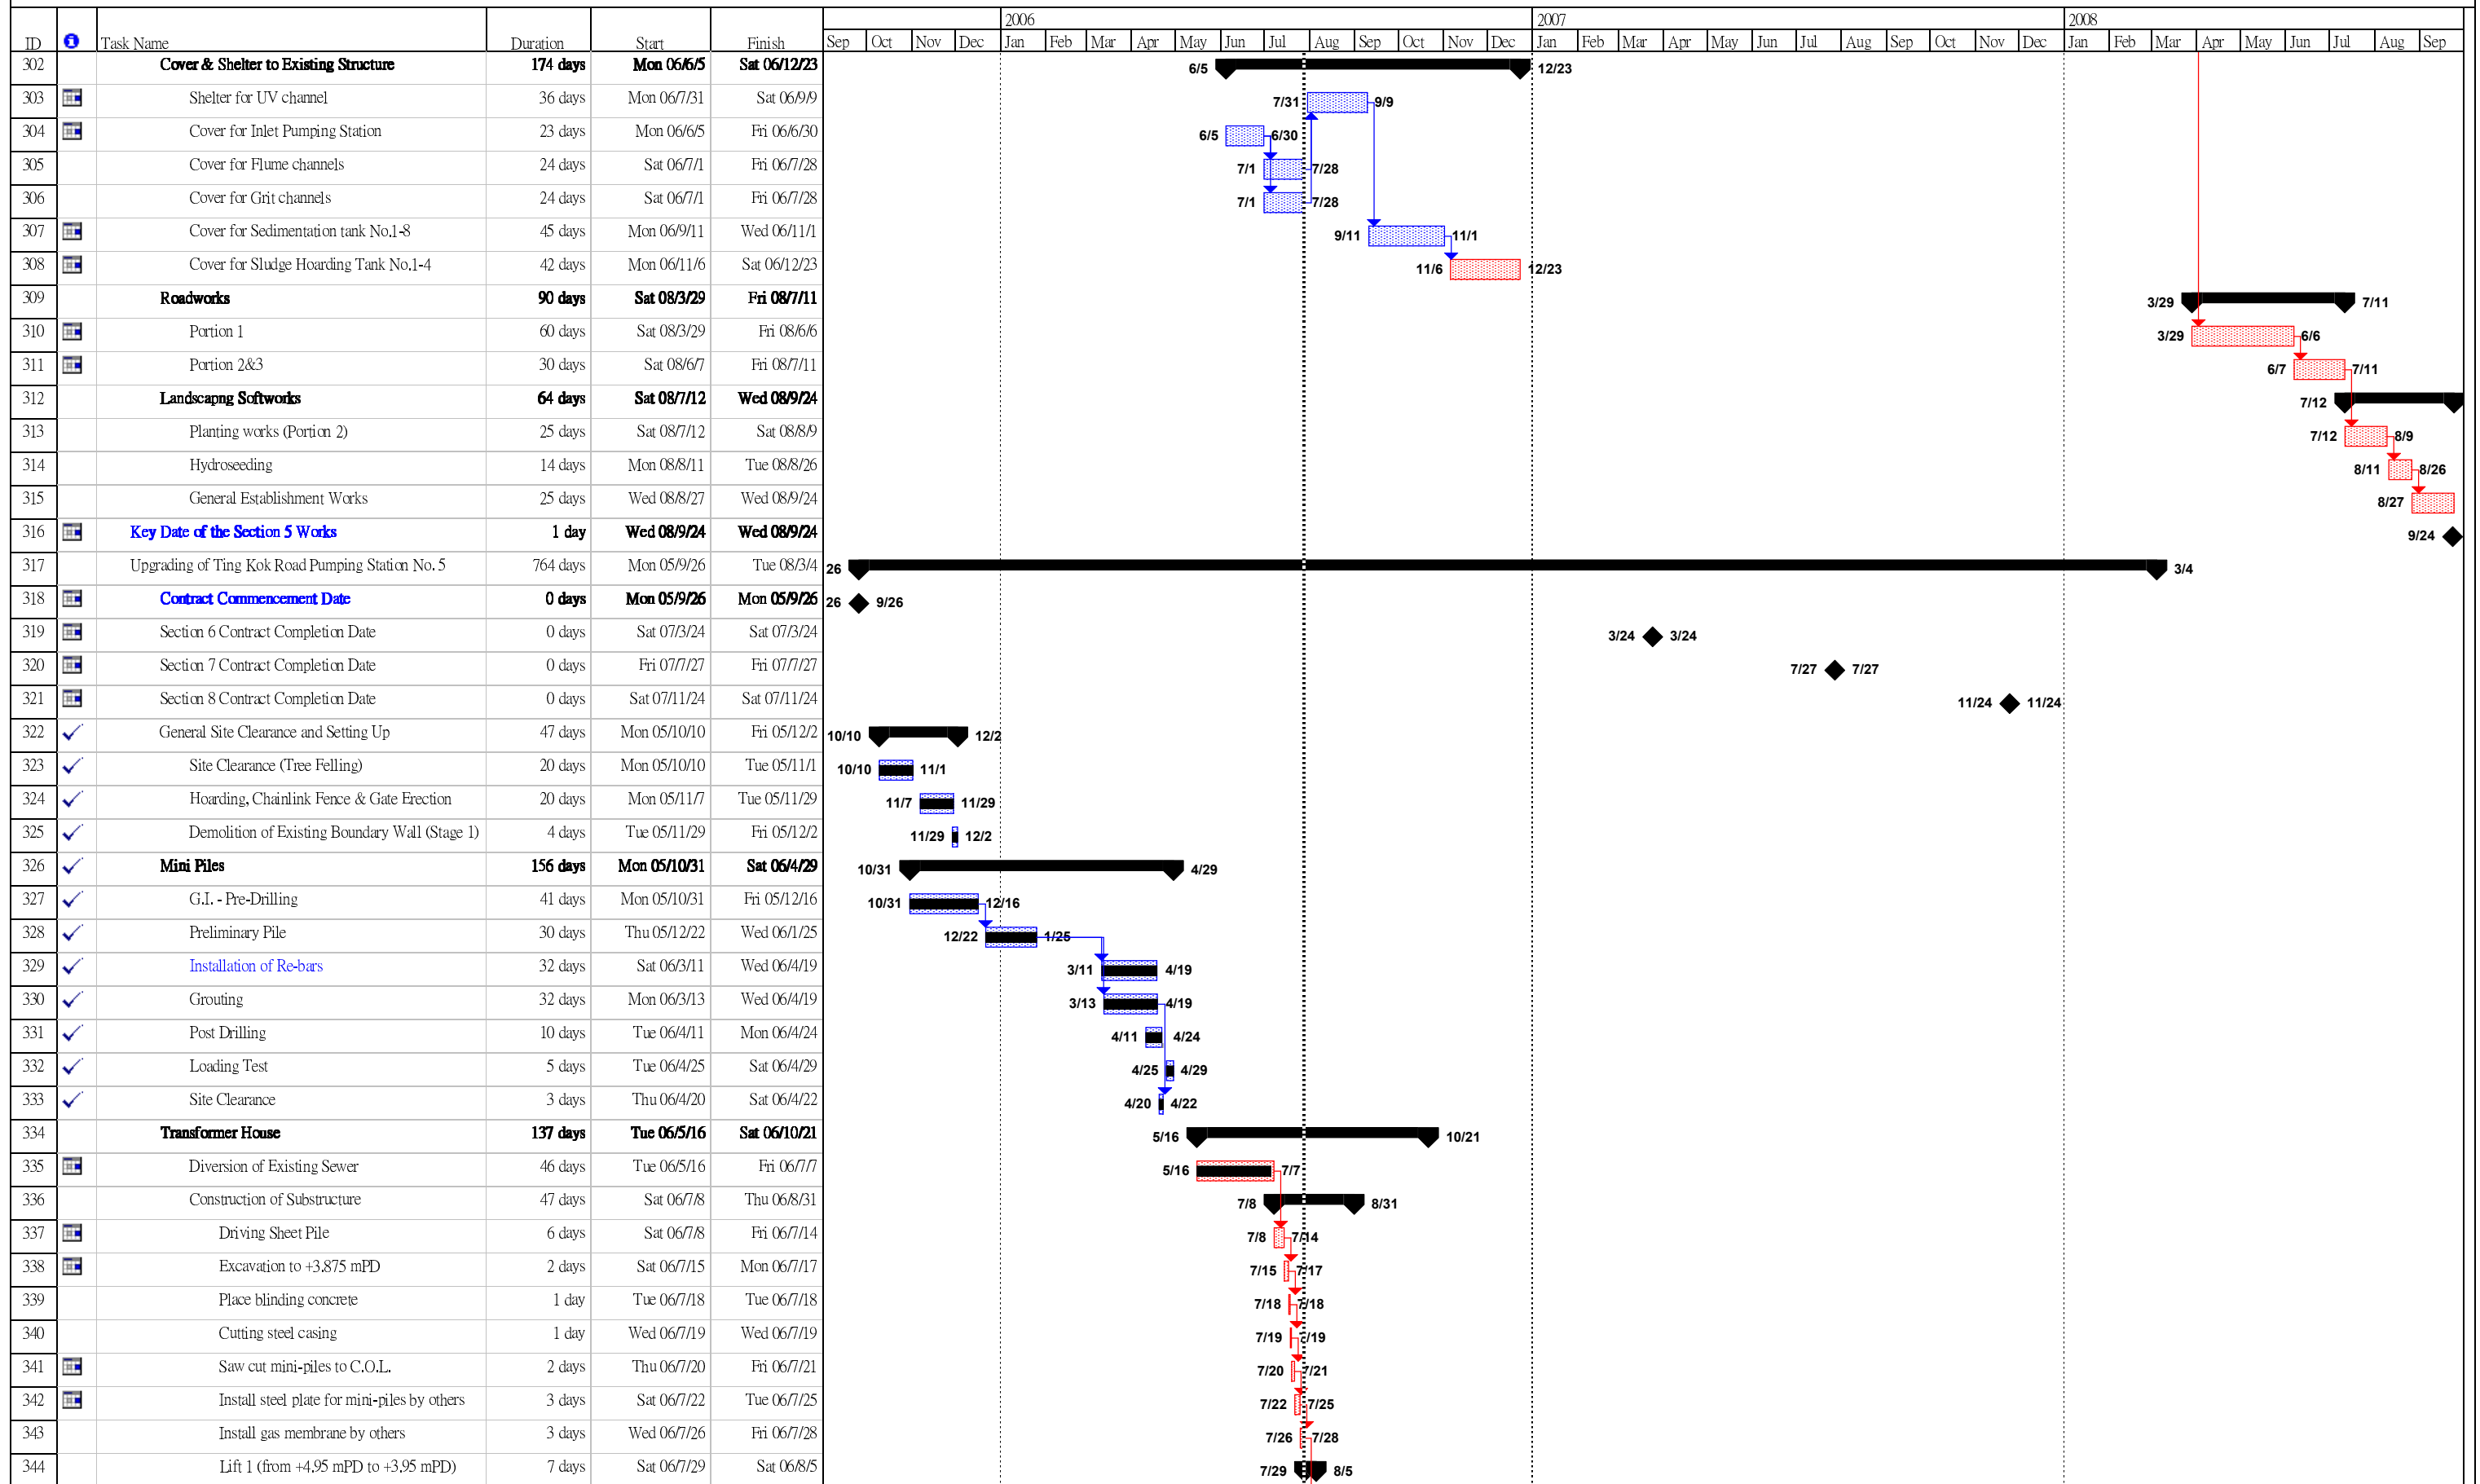

Date: Fri 06/7/28

Task		Progress		Summary		Rolled Up Critical Task		Rolled Up Progress		External Tasks	
Critical Task		Milestone		Rolled Up Task		Rolled Up Milestone		Split		Project Summary	



**Maeda Corporation**  
 Contract No. DC/2005/01  
 Expansion of Shek Wu Hui Sewage Treatment Works and  
 Upgrading of Ting Kok Road Pumping Station No.5  
**Master Programme (Rev. 2)**

ID	Task Name	Duration	Start	Finish	2006												2007												2008									
					Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
345	Erect external formwork	2 days	Sat 06/7/29	Mon 06/7/31										7/29	7/31																							
346	Steel fixing	2 days	Tue 06/8/1	Wed 06/8/2										8/1	8/2																							
347	Inspection and place concrete	1 day	Thu 06/8/3	Thu 06/8/3										8/3	8/3																							
348	Strike external formwork	2 days	Fri 06/8/4	Sat 06/8/5										8/4	8/5																							
349	Lift 2 (from +5.95 mPD to +3.95 mPD)	10 days	Mon 06/8/7	Thu 06/8/17										8/7	8/17																							
350	Erect internal formwork	2 days	Mon 06/8/7	Tue 06/8/8										8/7	8/8																							
351	Steel fixing	2 days	Wed 06/8/9	Thu 06/8/10										8/9	8/10																							
352	Erect external formwork	2 days	Fri 06/8/11	Sat 06/8/12										8/11	8/12																							
353	Inspection and place concrete	1 day	Mon 06/8/14	Mon 06/8/14										8/14	8/14																							
354	Strike internal and external formwork	2 days	Tue 06/8/15	Wed 06/8/16										8/15	8/16																							
355	SAND filling of void	1 day	Thu 06/8/17	Thu 06/8/17										8/17	8/17																							
356	Lift 3 (from +6.15 mPD to +5.95 mPD)	12 days	Fri 06/8/18	Thu 06/8/31										8/18	8/31																							
357	Steel fixing	1 day	Fri 06/8/18	Fri 06/8/18										8/18	8/18																							
358	Erect kicker formwork	2 days	Sat 06/8/19	Mon 06/8/21										8/19	8/21																							
359	Inspection and place concrete	1 day	Tue 06/8/22	Tue 06/8/22										8/22	8/22																							
360	Strike formwork	2 days	Wed 06/8/23	Thu 06/8/24										8/23	8/24																							
361	Backfill SAND up to EGL	2 days	Fri 06/8/25	Sat 06/8/26										8/25	8/26																							
362	Extract sheet piles	4 days	Mon 06/8/28	Thu 06/8/31										8/28	8/31																							
363	Construction of Superstructure	22 days	Fri 06/9/1	Tue 06/9/26										9/1	9/26																							
364	Lift 4 (from +11.20 mPD to +6.15 mPD)	13 days	Fri 06/9/1	Fri 06/9/15										9/1	9/15																							
365	Erect falsework and formwork for inter	4 days	Fri 06/9/1	Tue 06/9/5										9/1	9/5																							
366	Steel fixing	3 days	Wed 06/9/6	Fri 06/9/8										9/6	9/8																							
367	Erect external formwork	3 days	Sat 06/9/9	Tue 06/9/12										9/9	9/12																							
368	Inspection and place concrete	1 day	Wed 06/9/13	Wed 06/9/13										9/13	9/13																							
369	Strike external wall formwork	2 days	Thu 06/9/14	Fri 06/9/15										9/14	9/15																							
370	Lift 5 (from +12.30 mPD to +11.20 mPD)	7 days	Sat 06/9/16	Sat 06/9/23										9/16	9/23																							
371	Erect internal wall formwork for parap	2 days	Sat 06/9/16	Mon 06/9/18										9/16	9/18																							
372	Steel fixing	1 day	Tue 06/9/19	Tue 06/9/19										9/19	9/19																							
373	Erect external formwork	2 days	Wed 06/9/20	Thu 06/9/21										9/20	9/21																							
374	Inspection and place concrete	1 day	Fri 06/9/22	Fri 06/9/22										9/22	9/22																							
375	Strike formwork	1 day	Sat 06/9/23	Sat 06/9/23										9/23	9/23																							
376	Strike falsework and formwork	2 days	Mon 06/9/25	Tue 06/9/26										9/25	9/26																							
377	Internal Finishes (incl. Plumbing, cat ladder, etc.)	22 days	Wed 06/9/27	Sat 06/10/21										9/27	10/21																							
378	Pumping Station	341.5 days	Wed 06/5/3	Tue 07/6/5										5/3	6/5																							
379	General Excuvation & Trial Trench	5 days	Wed 06/5/3	Tue 06/5/9										5/3	5/9																							
380	Sheet Piling	50 days	Tue 06/5/9	Thu 06/7/6										5/9	7/6																							
381	ELS Works for Pumping Station No. 5	73 days	Thu 06/7/6	Fri 06/9/29										7/6	9/29																							
382	Excavate to +4.80 mPD	3 days	Thu 06/7/6	Mon 06/7/10										7/6	7/10																							
383	Install 1st layer of waling and struts	5 days	Mon 06/7/10	Sat 06/7/15										7/10	7/15																							
384	Place concrete between the sheetpile wall ar	3 days	Sat 06/7/15	Wed 06/7/19										7/15	7/19																							
385	Excavate to +2.10 mPD	7 days	Wed 06/7/19	Thu 06/7/27										7/19	7/27																							
386	Install 2nd layer of waling and struts	5 days	Thu 06/7/27	Wed 06/8/2										7/27	8/2																							
387	Place concrete between the sheetpile wall ar	3 days	Wed 06/8/2	Sat 06/8/5										8/2	8/5																							

Date: Fri 06/7/28

Task  Progress    
  Summary    
  Rolled Up Critical Task    
  Rolled Up Progress    
  External Tasks    
  Critical Task    
  Milestone    
  Rolled Up Task    
  Rolled Up Milestone    
  Split    
  Project Summary







