#### MONTHLY EM&A REPORT

ATAL-Degrémont-China State Joint Venture

Contract No. DC/2008/03 Design, Build and Operate Pillar Point Sewage Treatment Works: *Fourteenth Monthly EM&A Report* 

January 2012

**Environmental Resources Management** 

21/F Lincoln House 979 King's Road Taikoo Place Island East, Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

#### MONTHLY EM&A REPORT

ATAL-Degrémont-China State Joint Venture

## Contract No. DC/2008/03 Design, Build and Operate Pillar Point Sewage Treatment Works: *Fourteenth Monthly EM&A Report*

January 2012

Reference 0119806

| For and on behalf of                                     |
|--|
| ERM-Hong Kong, Limited                                   |
| Approved by: Frank Wan                                   |
| Signed: Marchatt   |
| Position: Partner  |
| Certified by:<br>(Environmental Team Leader – Winnie Ko) |
| Certified by:  |
| Date: <u>14 January 2012</u>                             |



AECOM 8/F Grand Central Plaza, Tower 2 138 Shatin Rural Committee Road Shatin, Hong Kong www.aecom.com

Your Ref: 60017423/C/jwym/12011303

#### By Hand & By Fax (2833 9162)

Drainage Services Department Sewage Services Branch Harbour Area Treatment Scheme Division 5/F., Western Magistracy, 2A Pok Fu Lam Road, Hong Kong.

Attn: Mr. Kenley C.K. KWOK (T: 2159 3409)

13 January 2012

Dear Sir,

Contract No. DC/2008/03 Design, Build and Operate Pillar Point Sewage Treatment Works

#### Monthly EM&A Report for December 2011

Reference is made to Environmental Team (ET)'s revised draft of the Monthly EM&A Report for December 2011 provided by email dated 13 January 2012. We have no further comment.

We hereby verify the said Monthly EM&A Report as having complied with the requirement as set out in the EM&A Manual in accordance with the condition 3.6 of Environmental Permit No. EP-321/2008.

Should you have any queries, please feel free to contact the undersigned at 3922 9393.

Yours faithfully,

For and on behalf of AECOM Asia Co. Ltd.

Y T Tang Independent Environmental Checker

c.c. AECOM – Mr. Tim Lee ERM – Ms. Winnie Ko ATAL–Degremont–China State JV – Mr. C.Y. Fong (Fax No. 2317 7609) (Fax No. 2723 5660) (Fax No. 2811 3321)

| 1     | INRODUCTION  | 1  |
|-------|--|----|
| 1.1   | Purpose of the Report                                      | 1  |
| 1.1   | STRUCTURE OF THE REPORT                                    | 1  |
| 1,2   | STRUCTURE OF THE REFORM                                    | 1  |
| 2     | PROJECT INFORMATION  | 3  |
| 2.1   | BACKGROUND   | 3  |
| 2.2   | GENERAL SITE DESCRIPTION                                   | 4  |
| 2.2   | Construction Activities                                    | 4  |
| 2.4   | PROJECT ORGANISATION AND MANAGEMENT STRUCTURE              | 4  |
| 2.4   | STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS                 | 5  |
| 2.0   |  |    |
| 3     | ENVIRONMENTAL MONITORING REQUIREMENTS                      | 6  |
| 3.1   | AIR QUALITY MONITORING                                     | 6  |
| 3.1.1 | Monitoring Location  | 6  |
| 3.1.2 | Monitoring Parameter and Frequency                         | 6  |
| 3.1.3 | Action and Limit Levels                                    | 6  |
| 3.1.4 | Monitoring Equipment                                       | 6  |
| 3.1.5 | Monitoring Methodology                                     | 7  |
| 3.1.6 | Event and Action Plan                                      | 9  |
| 3.2   | LANDSCAPE AND VISUAL MONITORING                            | 9  |
| 3.3   | ENVIRONMENTAL MITIGATION MEASURES AND ENVIRONMENTAL        |    |
|       | REQUIREMENTS IN CONTRACT                                   | 9  |
| 4     | IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION          | r  |
|       | REQUIREMENTS   | 10 |
| 5     | MONITORING RESULTS   | 11 |
| 5.1   | AIR QUALITY  | 11 |
| 6     | WASTE MANAGEMENT   | 12 |
| -     |  |    |
| 7     | ENVIRONMENTAL INSPECTIONS                                  | 13 |
| 7.1   | WEEKLY SITE AUDITS   | 13 |
| 7.2   | LANDSCAPE AND VISUAL MONITORING                            | 15 |
| 8     | ENVIRONMENTAL NON-CONFORMANCE                              | 16 |
| 8.1.1 | Summary of Monitoring Exceedance                           | 16 |
| 8.1.2 | Summary of Environmental Non-Compliance                    | 16 |
| 8.1.3 | Summary of Environmental Complaint                         | 16 |
| 8.1.4 | Summary of Environmental Summon and Successful Prosecution | 16 |
| 9     | FUTURE KEY ISSUES  | 17 |

| 9.1.1 | Key Issues for the Coming Month                         | 17 |
|-------|---|----|
| 9.1.2 | Monitoring Schedule for the Next Reporting Period       | 17 |
| 9.1.3 | <b>Construction Programme for the Next Three Months</b> | 17 |
| 10    | <b>REVIEW OF THE EM&amp;A DATA AND EIA PREDICTIONS</b>  | 18 |
| 10.1  | AIR QUALITY   | 18 |
| 10.2  | WASTE MANAGEMENT  | 18 |
| 10.3  | CONCLUSION OF REVIEW                                    | 19 |
| 11    | CONCLUSIONS   | 20 |

## LIST OF TABLES

| Table 2.1 | Summary of Construction Activities | Undertaken in Reporting Period |
|-----------|------------------------------------|--------------------------------|
|-----------|------------------------------------|--------------------------------|

- Table 2.2
   Summary of Environmental Licensing, Notification and Permit Status
- Table 3.1
   Construction Phase Air Monitoring Locations
- Table 3.2Construction Phase Air Quality Monitoring Parameters and Frequency
- Table 3.3Action and Limit Levels for Air Quality
- Table 3.4TSP Monitoring Equipment
- Table 6.1Quantities of Waste Generated from the Project
- Table 9.1
   Construction Works to be Undertaken in the Next Reporting Period
- Table 10.1
   Comparison of the HKAQO and Air Quality Monitoring Results
- Table 10.2Quantity of Actual Amount of C&D Materials, General Wastes and Chemical<br/>Wastes Generated and EIA Estimation

## LIST OF ANNEXES

| Annex A Location of Projec | Annex A | Location of Project |
|----------------------------|---------|---------------------|
|----------------------------|---------|---------------------|

- Annex B Works Location
- Annex C Project Organization Chart and Contact Detail
- Annex D Locations of Air Quality Monitoring Stations
- Annex E Monitoring Schedule of the Reporting Month and Next Month
- Annex F 24-hour and 1-hour TSP Monitoring Results
- Annex G Calibration Reports for HVSs
- Annex H Event / Action Plan for Air Quality Monitoring
- Annex I Implementation Schedule of Mitigation Measures
- Annex J Waste Flow Table
- Annex K Environmental complaint, Environmental Summons and Prosecution Log
- Annex L Construction Programme for the Project

## **EXECUTIVE SUMMARY**

The construction works of *DC/2008/03 of Design, Build and Operate Pillar Point Sewage Treatment Works (the Project)* commenced on 13 November 2010. This is the 14th monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the period from 1 to 31 December 2011 in accordance with the EM&A Manual.

## Summary of Construction Works undertaken during the Reporting Month

Works undertaken in the reporting month include:

- Backfilling at Admin Building;
- Constructing drainage pipe work at Admin Building;
- Excavation works at Sludge Dewatering Building;
- Constructing foundation at Sludge Dewatering Building; and
- Constructing wall at P2 CEPT and PTW area.

## Environmental Monitoring and Audit Progress

A summary of the monitoring activities undertaken in this reporting period is listed below:

- 24-hour TSP Monitoring at each monitoring station (AM1 and AM2) 6 sets
- 1-hour TSP Monitoring at each monitoring station (AM1 and AM2) 18 sets

5 times

- Joint Environmental Site Inspection
- Landscape & Visual Monitoring once

## Air Quality

6 sets of 24-hour TSP and 18 sets of 1-hr TSP measurements were carried out at each of the designated monitoring stations during the reporting period. No exceedance was recorded during the reporting period.

### Waste Management

Waste generated from this Project includes inert construction and demolition (C&D) materials (public fill) and non-inert C&D materials (construction wastes). A total of 3,011 tonnes of public fill were delivered to the fill bank. No plastic and paper/cardboard was recovered and 20 kg of metals were sent to recyclers in the reporting period. 17.14 tonnes general refuse was disposed of in the reporting period. No chemical waste was disposed of in the reporting period.

Five weekly joint environmental site inspections were carried out by the representatives of the Contractor, the SOR and the Environmental Team (ET). Details of the audit findings and implementation status of the mitigation measures are presented in *Section 7.1*.

#### Landscape & Visual

Review on landscape and visual mitigation measures was performed on 30 December 2011. Details of the audit findings and implementation status of the mitigation measures are presented in *Sections 3.2* and 7.2.

# Environmental Exceedance/Non-conformance/Compliant/Summons and Prosecution

No exceedance was recorded during the reporting period.

No non-compliance event was recorded during the reporting period.

No environmental complaint and summon/prosecution was received in this reporting period.

### Future Key Issues

Works to be undertaken in the next reporting month include:

- Constructing drainage pipe work at Admin Building;
- Constructing foundation at Sludge Dewatering Building;
- Constructing wall at P2 CEPT and PTW area; and
- Excavation at Electrical Building No.1.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoff, waste management and landscaping issues.

## 1 INRODUCTION

ERM-Hong Kong, Limited (ERM) was appointed by ATAL – Degrémont – China State Joint Venture (ADC-JV) (the Contractor) as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the *Contract No. DC/2008/03 of Design, Build and Operate Pillar Point Sewage Treatment Works (the Project).* 

## 1.1 PURPOSE OF THE REPORT

This is the 14th EM&A report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from **1** to **31 December 2011**.

### **1.2** STRUCTURE OF THE REPORT

The structure of the report is as follows:

Section 1 : **Introduction** details the scope and structure of the report.

### Section 2: Project Information

summarises background and scope of the Project, site description, project organization, construction programme, the construction works undertaken and the status of Environmental Permits (EP)/licences over the construction phase of the Project.

### Section 3: Environmental Monitoring Requirements

summarises the environmental monitoring including monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event/Action Plans, environmental mitigation measures as recommended in the approved EIA report, EP and relevant environmental requirements stated in the Contract Specification.

- Section 4 : **Implementation Status on Environmental Mitigation Measures** summarises the implementation of environmental protection measures during the reporting period.
- Section 5 : **Monitoring Results** summarises the monitoring results obtained in the reporting period.

## Section 6 : Waste Management summarises the quantity of public fill and construction waste generated in the reporting period

## Section 7: Environmental Site Inspection

summarises the audit findings of the weekly site inspections undertaken within the reporting period.

## Section 8: Environmental Non-conformance

summarises any exceedance of environmental performance standard, and environmental complaints and environmental summons received within the reporting period.

### Section 9: Further Key Issues

summarises the impact forecast and monitoring schedule for the next reporting month.

## Section 10 : Review of the EM&A Data and Predictions

compares the monitoring data and waste quantity against predictions in the approved Project EIA report.

Section 11 : Conclusions

#### 2.1 BACKGROUND

The existing Pillar Point Sewage Treatment Works (PPSTW) is located to the north of the Tuen Mun River Trade Terminal and is abutting the Lung Mun Road to its north. It is a preliminary treatment works with screening and grit removal processes with treated effluent discharged to the sea (North Western Water Control Zone) via a twin submarine outfall. The *Review of the Tuen Mun and Tsing Yi Sewerage Master Plan* (RTMTYSMP) commissioned in February 1999, recommended to expand the sewage treatment capacity and to upgrade the plant to chemically enhanced primary treatment (CEPT) with disinfection in order to cater for the projected ultimate population and planned developments in the Tuen Mun area, and to improve the effluent quality and hence to reduce pollution loadings to the receiving waters.

The upgrading of the PPSTW comprises the following works:

- expanding the treatment capacity of the existing PPSTW to cope with the increased peak wet-weather sewage flow in Tuen Mun area;
- upgrading the sewage treatment level of the existing PPSTW to incorporate chemical treatment with disinfection at minimum removal rates of 70%, 55% and 99.9% of suspended solids (SS), biochemical oxygen demand (BOD) and *E.coli*, respectively;
- upgrading existing septic waste reception facilities at PPSTW; and
- providing and upgrading ancillary facilities including the administration building, workshop, laboratory, odour control facilities, sludge handling and dewatering facilities, access roads and minor landscaping works within the STW for the operation and maintenance of the upgraded STW.

The potential environmental impacts of the Project have been studied in the "Upgrading of Pillar Point Sewage Treatment Works" (EIAO Register No: AEIAR-145/2008). The EIA was approved on 10 June 2008 under the Environmental Impact Assessment Ordinance (EIAO) and an Environmental Permit (EP-321/2008) for the works was granted on 17 November 2008. Under the requirements of Condition 3.1 of EP-322/2008, an EM&A programme as set out in the EM&A Manual is required to be implemented.

The construction works commenced on 13 November 2010 and are scheduled for completion by 2014.

## 2.2 GENERAL SITE DESCRIPTION

The open area adjacent to the existing PPSTW has been designated for the upgrading works. The layout of the upgrading works is illustrated in *Annex A*.

## 2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in the reporting period is shown in *Table 2.1*. The locations of the construction activities are shown in *Annex B*. The construction programme of the Project in the reporting month and the upcoming 3 months is presented in *Annex L*.

## Table 2.1 Summary of Construction Activities Undertaken in Reporting Period

#### Construction Activities Undertaken

- Backfilling at Admin Building;
- Constructing drainage pipe work at Admin Building;
- Excavation works at Sludge Dewatering Building;
- Constructing foundation at Sludge Dewatering Building; and
- Constructing wall at P2 CEPT and PTW area.

#### 2.4 PROJECT ORGANISATION AND MANAGEMENT STRUCTURE

The project organization chart and contact details are shown in *Annex C*.

#### 2.5 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the valid permits, licences, and/or notifications on environmental protection for this Project is presented in *Table 2.2*.

## Table 2.2 Summary of Environmental Licensing, Notification and Permit Status

| Permit/ Licences/     | Reference       | Validity Period   | Remarks                 |
|-----------------------|-----------------|-------------------|-------------------------|
| Notification          |                 |                   |                         |
| Environmental         | EP-321/2008     | Throughout the    | Permit granted on 17    |
| Permit                |                 | Contract          | November 2008.          |
| Notification of       | Ref No. 308136  | Throughout the    | -                       |
| Construction Works    |                 | Contract          |                         |
| under Air Pollution   |                 |                   |                         |
| Control (Construction |                 |                   |                         |
| Dust) Regulation      |                 |                   |                         |
| Water Discharge       | WT00008027-     | Till 31 December  | Wastewater discharge    |
| License               | 2010            | 2015              | licence was issued by   |
|                       |                 |                   | EPD on 7 December 2010. |
| Construction Noise    | GW-RW0471-11    | 28 July 2011 – 27 |                         |
| Permit                |                 | January 2012      | -                       |
|                       |                 |                   |                         |
| Chemical Waste        | 5213-421-A2620- | Throughout the    | Licence approved on 28  |
| Producer Registration | 01              | Contract          | October 2010            |

## 3 ENVIRONMENTAL MONITORING REQUIREMENTS

## 3.1 AIR QUALITY MONITORING

## 3.1.1 Monitoring Location

The proposed air quality monitoring stations for the construction phase of the Project, as recommended in the approved EM&A Manual, are given in *Table 3.1* and shown in *Annex D*. The proposed locations (AM1 and AM2) have been agreed with the Drainage Services Department (DSD), Environmental Protection Department (EPD) and the Independent Environmental Checker (IEC).

## Table 3.1Construction Phase Air Monitoring Locations

| Monitoring ID | Air Quality Monitoring Station          |
|---------------|---|
| AM1           | Tuen Mun EMSD Servicing Vehicle Station |
| AM2           | River Trade Terminal Office             |

## 3.1.2 Monitoring Parameter and Frequency

The construction phase air quality monitoring has been conducted at the designated monitoring stations in accordance with the requirements stipulated in the EM&A Manual. 1-hour and 24-hour TSP levels have been monitored at the frequency and duration stated in *Table 3.2*. The construction phase TSP monitoring has been conducted as per the schedule presented in *Annex E*.

### Table 3.2 Construction Phase Air Quality Monitoring Parameters and Frequency

| Parameter   | Frequency            |  |
|-------------|----------------------|--|
| 24-hour TSP | Once every 6 days    |  |
| 1-hour TSP  | 3 times every 6 days |  |

### 3.1.3 Action and Limit Levels

The Action and Limit levels have been established and presented in Table 3.3.

### Table 3.3Action and Limit Levels for Air Quality

| Parameter   | Air Monitoring Station | Action Level, µgm-3 | Limit Level, µgm <sup>-3</sup> |
|-------------|------------------------|---------------------|--------------------------------|
| 24-hour TSP | AM1                    | 183                 | 260                            |
|             | AM2                    | 192                 | 260                            |
| 1-hour TSP  | AM1                    | 343                 | 500                            |
|             | AM2                    | 383                 | 500                            |

### 3.1.4 Monitoring Equipment

Continuous 24-hour and 1-hour TSP monitoring were performed using High Volume Samplers (HVS) with appropriate sampling inlets installed, located at the designated monitoring stations.

The performance specification of HVS complied with the standard method "Determination of Suspended Particulate Matter in the Atmosphere (High Volume Method)" as stipulated in US EPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50 Appendix B). Table 3.4 summarises the equipment that were deployed for the 24-hour and 1-hour TSP monitoring respectively.

## Table 3.4TSP Monitoring Equipment

| Monitoring Station | Monitoring Equipment (HVS and Calibrator)       |
|--------------------|---|
| 24-hr and 1-hr TSP |   |
| AM1                | GMW GS-2310 (S/N 7580), CM-AIR-43 (S/N 9833620) |
| AM2                | GMW GS-2310 (S/N 1252), CM-AIR-43 (S/N 9833620) |

## 3.1.5 Monitoring Methodology

The setup locations of the HVSs at monitoring stations were listed in *Table 3.1*. All HVSs were free-standing with no obstruction.

The following criteria were considered in the installation of the HVSs:

- appropriate support to secure the samplers against gusty wind were provided at AM1 and AM2;
- a minimum of 2m separation from walls, parapets and penthouses was required for rooftop samplers;
- no furnace or incinerator flues were nearby;
- airflow around the sampler was unrestricted; and
- permission was obtained to set up the samplers and to gain access to the monitoring stations.

### Preparation of Filter Papers

- glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected;
- all filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25°C and not variable by more than ± 3°C; the relative humidity (RH) was 40%; and
- SGS Hong Kong Ltd, a HOKLAS accredited laboratory, implements comprehensive quality assurance and quality control programmes.

### Field Monitoring

• the power supply was checked to ensure that the HVSs were working properly;

- the filter holder and the area surrounding the filter were cleaned;
- the filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;
- the filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- the swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- then the shelter lid was closed and secured with the aluminium strip;
- the HVSs were warmed-up for about 5 minutes to establish runtemperature conditions;
- a new flowrate record sheet was set into the flow recorder;
- the flow rates of the HVSs were checked and adjusted to between 1.22 1.37 m<sup>3</sup>min<sup>-1</sup> which were within the range specified in the EM&A Manual (ie 0.6 1.7 m<sup>3</sup>min<sup>-1</sup>);
- the programmable timer was set for a sampling period of 24 hours ± 1 hour, and the starting time, weather condition and the filter number were recorded;
- the initial elapsed time was recorded;
- at the end of sampling, the sampled filter was removed carefully and folder in half length so that only surfaces with collected particulate matter were in contact;
- it was then placed in a clean plastic envelope and sealed;
- all monitoring information was recorded on a standard data sheet; and
- filters were sent to SGS Hong Kong Ltd for analysis.

## Maintenance and Calibration

- the HVSs and their accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply; and
- the flow rate of each HVS with mass flow controller were calibrated using an orifice calibrator. Initial calibrations of the dust monitoring equipments were conducted upon installation and prior to commissioning. Five-point calibration was carried out for HVSs using CM-AIR-43 Calibration Kit. HVSs are calibrated on a bi-monthly basis. The calibration records for the HVSs are given in *Annex G*.

## Wind Data Monitoring

Average wind data (wind speed and wind direction) during the monitoring period were obtained from the meteorological station at Tuen Mun of the Hong Kong Observatory (HKO) and were presented in *Annex F*.

## 3.1.6 Event and Action Plan

The Event/Action Plan (EAP) for air quality monitoring is presented in *Annex H*.

## 3.2 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, monthly landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures recommended in the approved EIA Report are fully achieved. The monitoring procedures and criteria as described in the EM&A Manual were adopted.

## 3.3 ENVIRONMENTAL MITIGATION MEASURES AND ENVIRONMENTAL REQUIREMENTS IN CONTRACT

All relevant environmental mitigation measures listed in the EIA Report and the EM&A Manual as well as the specific environmental requirements stated in Contract Specification are summarised in *Annex I*. A summary of the key environmental mitigation measures implemented as per the Contract Requirements is also presented in *Annex I*.

# IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS

The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Report, EM&A Manual and EP. The implementation status of the measures during the reporting period is summarised in *Annex I*.

#### 5.1 AIR QUALITY

A total of 6 sets of 24-hour and 18 sets of 1-hour TSP measurements have been taken at each of the monitoring stations (AM1 and AM2) during the reporting period. The monitoring data for 24-hour TSP and 1-hour TSP together with wind data and graphical presentations for the past 4 months are presented in *Annex F*. The weather conditions during the monitoring period ranged from Sunny to Cloudy. The local impacts near the monitoring stations of AM1 and AM2 were mainly associated with vehicular emissions. No exceedance of Action and Limit Level of 1-hr and 24-hr TSP was recorded during the reporting period.

Wastes generated from this Project include inert construction and demolition (C&D) materials (public fill) and non-inert C&D materials (construction waste). Construction waste comprises of general refuse, metals and paper/cardboard packaging materials. Metals generated from the Project are also grouped into construction waste as the materials were not disposed of with others at public fill. Reference has been made to the Monthly Summary Waste Flow Table prepared by the Contractor (*Annex J*). With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in *Table 6.1* below. The public fill and construction waste generated from the Project have been disposed of at the Tuen Mun Area 38 Fill Bank and WENT Landfill, respectively. No plastic and paper/ cardboard packing was sent to recyclers for recycling during the reporting period.

#### Table 6.1Quantities of Waste Generated from the Project

| Month / Year Quantity |  |  |                                  |
|-----------------------|--|--|----------------------------------|
|                       | C&D Materials Disposed<br>of at Public Fill (inert) <sup>(a)</sup> | C&D Materials Disposed of at<br>Landfill (Non-inert) | Chemical<br>Waste <sup>(d)</sup> |
|                       |  | (Construction waste) <sup>(b) (c)</sup>              |                                  |
| December 2011         | 3,011 tonnes   | 17.14 tonnes   | 0 L                              |

Notes:

(a) Inert C&D materials (public fill) include bricks, concrete, building debris, rubble and excavated soil. Total 3,011 tonnes of public fill were generated and were disposed of at the Tuen Mun Area 38 Fill Bank.

(b) Non-inert C&D materials (construction wastes) include metals, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Metals generated from the Project are grouped into construction wastes as the materials were not disposed of with others at the public fill. 17.14 tonnes of general refuse is recorded in the reporting month. Construction wastes other than metals and paper/cardboard packaging were disposed of at WENT Landfill. No plastic and paper/cardboard packaging was recovered and 20 kg of metals were recovered and sent to recyclers for recycling during the reporting period.

- (c) General refuse was disposed of at WENT by subcontractors.
- (d) Chemical waste was collected though the licensed chemical waste collector, Dunwell Ind. (Holdings) Ltd, with the waste collection licence number 7111-757-W0015-WC.

## 7 ENVIRONMENTAL INSPECTIONS

## 7.1 WEEKLY SITE AUDITS

Joint site inspections were conducted by representatives of the Contractor, SOR and the ET on 2, 9, 15, 22 and 30 December 2011. The IEC was also present at the joint inspection on 2 December 2011. There was no non-compliance recorded during the site inspections.

Major observations during the reporting period were summarised as follows:

## 2 December 2011

- Stagnant water was still observed in the concreted pit in PTW area. Moss and insect were observed in the stagnant water. The Contractor was seriously reminded to remove the stagnant water immediately.
- A pile of exposed sand and excavated soil was observed stored at PTW near Gate 3. The Contractor was reminded to wet the dusty materials or cover the materials with tarpaulin sheet within 3 working days to avoid generation of dust.
- Stagnant ground water was still observed at CEPT east corridor. Moss was observed in the water. The Contractor was reminded to remove the stagnant ground water immediately.
- Haul road along works area near Gate no. 2 was dry and dusty. Although water sprinklers were installed along the haul road, they were not in operation. The Contractor was recommended to operate the water sprinklers regularly to suppress the fugitive dust emission.
- Damage at the root (N44) and cavity at the main branch (T384 and N44) were observed at the retaining tree N44 and transplanted tree T384 in STW and Portion T1. Also, the transplanted tree N83 in Portion T1 was found in poor condition. The Contractor was reminded to keep checking the health status of the trees and seek advice from certified arborist for proper mitigation measures to be implemented.

### 9 December 2011

- Stagnant water was observed in concreted pit at Admin Building work site and in drainage channel at south haul road. The Contractor was reminded to remove the stagnant water to avoid breeding of mosquito.
- A pile of exposed sand and excavated soil was observed stored at PTW near Gate 3. The Contractor was reminded to wet the dusty materials or cover the materials with tarpaulin sheet within 3 working days to avoid generation of dust.
- Retained tree no. T08 was observed damaged. Broken branches were observed underneath. The Contractor was reminded to monitor their workers works especially lifting works and remind the workers to avoid damaging the trees.

## 15 December 2011

- Dusty exposed ground surface was observed at P2 CEPT worksite. The Contractor was reminded to wet the dusty materials or to cover the materials with tarpaulin sheet within 3 working days to avoid generation of fugitive dust.
- Concrete water was observed entering the storm drain near Gate 3. The Contractor was reminded to provide sand bags to avoid concrete water from entering the storm drain within 3 working days.
- Stagnant water and general refuse was observed in the concreted pit at P2 CEPT worksite. The Contractor was reminded to remove the stagnant water and general refuse within 3 working days.

## 22 December 2011

- Slope with exposed soil was observed at P2 CEPT worksite. The Contractor was reminded to wet the dusty materials or to cover the materials with tarpaulin sheet within 3 working days to avoid generation of fugitive dust.
- Concrete water was observed entering the storm drain near Gate 3. The Contractor was reminded to remove the concrete water immediately and provide sand bags to avoid concrete water from further entering the storm drain within 3 working days.
- Stagnant water and general refuse was observed at concreted pit at P2 CEPT worksite. The Contractor was reminded to remove the stagnant water and the general refuse within 3 working days.

## 30 December 2011

- Stagnant water was observed in the concreted pit at the Admin Building worksite and the wheel washing bay. The Contractor was reminded to remove the stagnant water to avoid breeding of mosquito.
- A pool of water and general refuse was observed at the P2 CEPT worksite. Contractor explained that the water was slowly moving to the low level at the north of the worksite for pumping out to water treatment. However, the Contractor was reminded to maintain a good housekeeping practice and clear the refuse within 3 working days.
- The tarpaulin sheets covering the excavated soil stored at the stockpiling area was observed loosely attached or broken. The Contractor was reminded to cover the exposed soil properly within 3 working days.

Follow-up actions were undertaken as reported by the Contractor and observed in the next weekly site inspections conducted in the reporting period.

#### 7.2 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, monthly landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures recommended in the EIA Report are fully achieved. A review of landscape and visual mitigation measures was performed on 30 December 2011. It was confirmed that most of the necessary landscape and visual mitigation measures as summarised in *Annex I* were implemented by the Contractor. The major findings were summarised as follow:

#### 30 December 2011

- For R85 and R86, cavities were found on root, crown and main trunk. There were decay on root, crown, trunk and branches. Dead branches were serious. Root decay was also found in N44. It is recommended that these trees are to be inspected by the Contractor's certified arborist ASAP and remediation actions should be taken as per the arborist's recommendations to avoid potential danger of falling.
- T181 has been found to be severely leaning. The Contractor was recommended to provide external support ASAP, the details of supporting should be advised by the Contractor's tree specialist/landscape subcontractor.
- Tree labels were missing for T264 and T262. The Contractor was advised to put back the tree labels within 3 working days.
- It is recommended to clear all the weeds, garbage and broken branches within the tree protection zones (e.g. T06, T08, T29, T62, T179 and T182).
- R59 was found to be infected by diseases. It is recommended that it should be inspected by the Contractor's certified arborist ASAP and remediation actions should be undertaken as per the arborist's recommendations to avoid spreading of the disease.

The Contractor was reminded to implement the follow-up actions and that the status of the follow-up actions will be reviewed in the first weekly site inspections in the next reporting period.

Key landscape and visual mitigation measures implemented in the reporting period include:

- Set up of a temporary tree nursery;
- Control dust and erosion of exposed soil;
- Stockpiling of topsoil for future reuse;
- Maintain existing tree record inventory; and
- Re-use existing top soil for new planting areas.

## 8 ENVIRONMENTAL NON-CONFORMANCE

## 8.1.1 Summary of Monitoring Exceedance

No exceedances of Action and Limit Levels of 1-hr and 24-hr TSP were recorded during the reporting period.

## 8.1.2 Summary of Environmental Non-Compliance

No non-compliance event was recorded during the reporting period.

### 8.1.3 Summary of Environmental Complaint

No complaint was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex K*.

### 8.1.4 Summary of Environmental Summon and Successful Prosecution

No summon was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex K*.

## 9 FUTURE KEY ISSUES

## 9.1.1 Key Issues for the Coming Month

Works to be undertaken for the coming monitoring period are summarised in *Table 9.1* below.

### Table 9.1 Construction Works to be Undertaken in the Next Reporting Period

| _  |  |
|----|--|
| Wo | ork to be taken  |
| ٠  | Constructing drainage pipe work at Admin Building;     |
| ٠  | Constructing foundation at Sludge Dewatering Building; |
| •  | Constructing walls at P2 CEPT and PTW area; and        |
|    |  |

• Excavation at Electrical Building No.1.

Potential environmental impacts arising from the above construction activities will mainly be associated with dust, construction noise, site runoff, waste management and landscaping issues.

#### 9.1.2 Monitoring Schedule for the Next Reporting Period

The tentative schedule of TSP monitoring for the next reporting period was presented in *Annex E*. Environmental monitoring will be conducted at the same monitoring locations in the next reporting period. The monitoring programme has been reviewed and was considered adequate to cater for the nature of works in progress.

### 9.1.3 Construction Programme for the Next Three Months

The most updated construction programme for the Project is presented in *Annex L*.

#### 10.1 AIR QUALITY

10

Since the EIA has included only qualitative assessment of dust impact during construction phase, a comparison was made between the monitoring results from the start of the Project and the Hong Kong Air Quality Objectives (HKAQO) (*Table 10.1*).

#### Table 10.1 Comparison of the HKAQO and Air Quality Monitoring Results

| Monitoring Station | HKAQO, ugm <sup>-3</sup><br>24 hour <sup>(1)</sup> | Measured 24-hour TSP Monitoring<br>Results, ugm <sup>-3 (a) (b)</sup> |          |
|--------------------|--|---|----------|
|                    |  | Average   | Range    |
| AM1                | 260  | 73  | 59 - 100 |
| AM2                | 260  | 81  | 60 - 102 |
| Notes:             |  |   |          |

(a) Only 24-hour TSP monitoring results were compared as there is no 1 hour TSP criterion in HKAQO.

(b) Average and range of data were calculated between the commencement of construction works and this reporting month.

The monitoring results show that the average and range of 24-hour TSP levels recorded since the commencement of the construction works have been well below the 24-hour TSP criterion in the HKAQO. Recommended mitigation measures in *Section 3.7.1.1* of EIA have been implemented throughout the construction period and were considered effective.

### **10.2** WASTE MANAGEMENT

The estimated amount of waste generated in this Project and the accumulated quantities of waste generated up to this reporting month are presented in *Table 10.2*. The amount of inert C&D material sent to public fills is larger than the estimated amount in EIA. With reference to the C&D Material Assessment (Contractor's General Submission (CSF) No.: DC200803/CSF/SAF/060026/A), the difference in quantity is mainly due to differences in excavation depths and excavation methods in the Contract Works and that assumed in the Reference Design. Recommended mitigation measures in *Sections 7.5.1.1* to *7.5.1.9* of the EIA will continue to be implemented during the construction stage.

| Type of Material               | Estimated Amount of<br>Public Fill and<br>Construction Waste<br>in EIA<br>(inert & non-inert) | Estimated Amount of<br>Public Fill and<br>Construction Waste<br>in C&D Material<br>Assessment (CSF No.:<br>DC200803/CSF/SAF/0<br>60026/A) <sup>(c)</sup> | Accumulated Actual<br>Amount of Public Fill<br>and Construction<br>Waste Recorded <sup>(a) (b)</sup><br><sup>(d)</sup> (inert & non-inert) |
|--------------------------------|---|--|--|
| Amount of C&D                  | 61,489 m <sup>3</sup>   | 77,600 m <sup>3</sup>  | 79,681 m <sup>3</sup>  |
| Materials Arising              |   |  |  |
| Amount of C&D                  | -   | -  | 3,164 m <sup>3</sup>   |
| Materials Reused on other site |   |  |  |
| Amount of C&D                  | 14,926 m <sup>3</sup>   | 18,000 m <sup>3</sup>  | 0 m <sup>3</sup>   |
| Materials Reused on site       |   |  |  |
| Amount of C&D                  | 46,563m <sup>3</sup>  | 59,600 m <sup>3</sup>  | 76,517 m <sup>3</sup>  |
| Materials Sent to              |   |  |  |
| Public Fills                   |   |  |  |
| General Refuse                 | Small   | -  | 174.63 tonnes  |
| Chemical Waste                 | Small   | -  | 810 L  |

## Table 10.2Quantity of Actual Amount of C&D Materials, General Wastes and Chemical<br/>Wastes Generated and EIA Estimation

Notes:

(a) The actual amount of C&D Materials was recorded since the commencement of construction works.

(b) The density of soil and rock (bulked) is  $1.8 \text{ tonnes}/\text{m}^3$ .

(c) The estimated amount of C&D material generated from the Contract Works was revised in the C&D Material Assessment and submitted to the SO on 9 September 2010 (CSF No.: DC200803/CSF/SAF/060026/A) due to the new plant & facility layout.

(d) The waste flow data for April and May 2011 was updated in August 2011 based on SOR's comments and has been confirmed by the Contractor. The waste flow data for August, September and November 2011 was updated in October, November and December 2011 respectively based on Contractor's revised waste flow summary. Detail of changes is shown in Annex J.

## 10.3 CONCLUSION OF REVIEW

The EIA predictions and the monitoring results since the commencement of construction works have been reviewed. The EIA concluded that the Project would not cause adverse impacts to the environment, and the monitoring results have also indicated the same so far. Mitigation measures recommended in the EP, EIA and EM&A Manual will continue to be implemented throughout the construction phase of the Project.

#### CONCLUSIONS

11

This EM&A Report presents the EM&A programme undertaken during the reporting period from 1 to 31 December 2011 in accordance with EM&A Manual and requirements of EP (EP-321/2008).

No exceedance of Action and Limit Levels of 24-hour TSP and 1-hour TSP was recorded at the monitoring stations during the reporting period.


Monthly landscape and visual monitoring was conducted in the reporting period. Most of the necessary landscape and visual mitigation measures recommended in the EIA Report were implemented by the Contractor. Follow-up actions are required by the Contractor to improve protection measures on the retained or to-be transplanted trees.

No non-compliance event was recorded during the reporting period.

No complaint and summons/prosecution was received during the reporting period.


The ET will keep track of the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures in the coming periods. Annex A

Location of Project

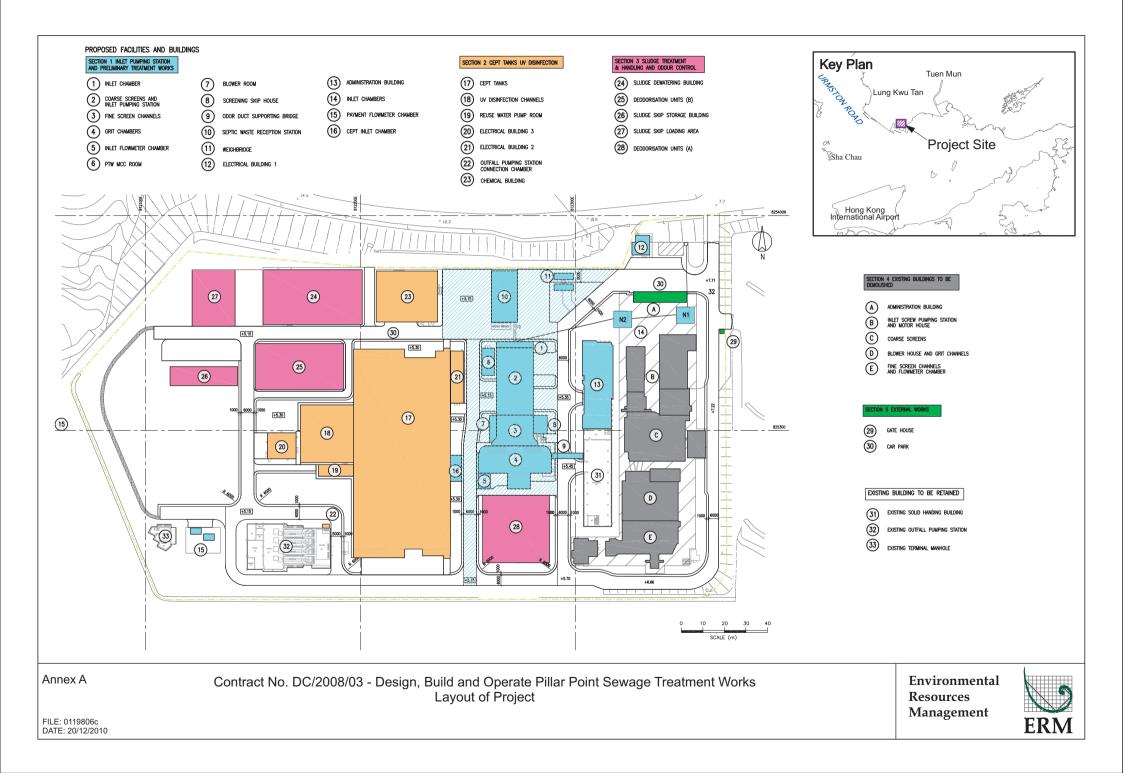

Annex B


Works Location

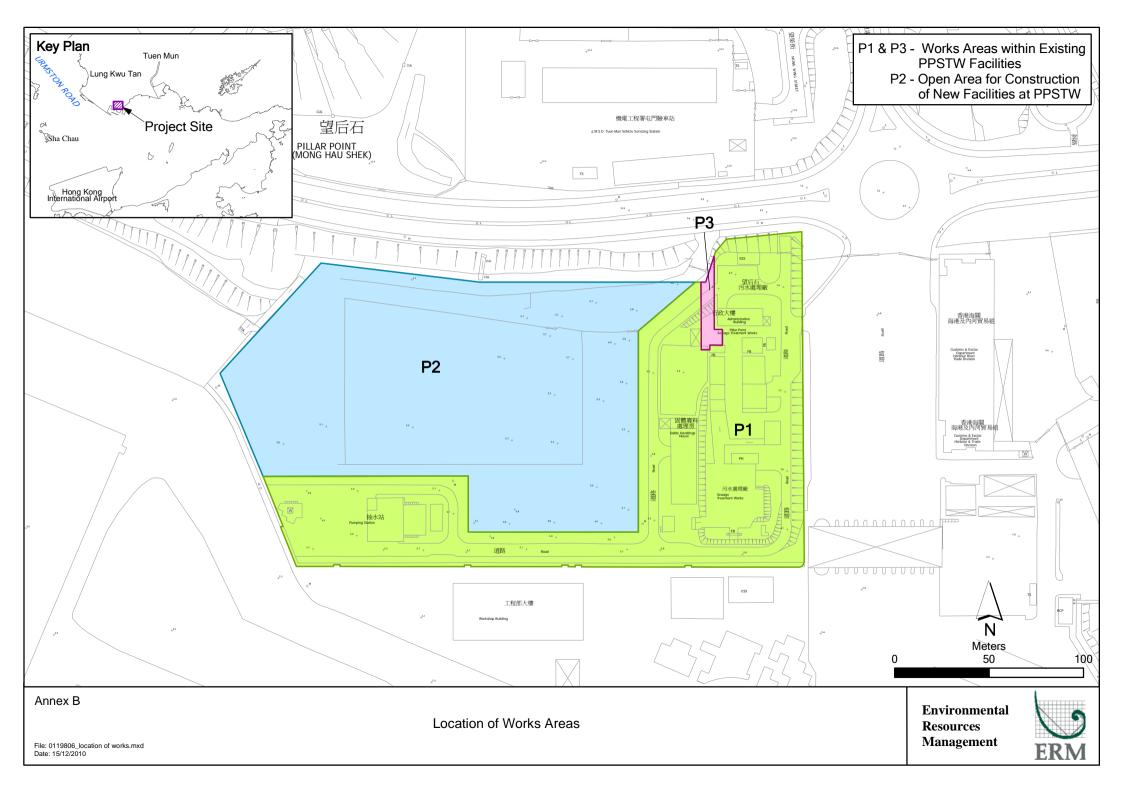

Annex C


Project Organization Chart with Contact Details

<u>Project Organization During Construction Phase (with contact details)</u>

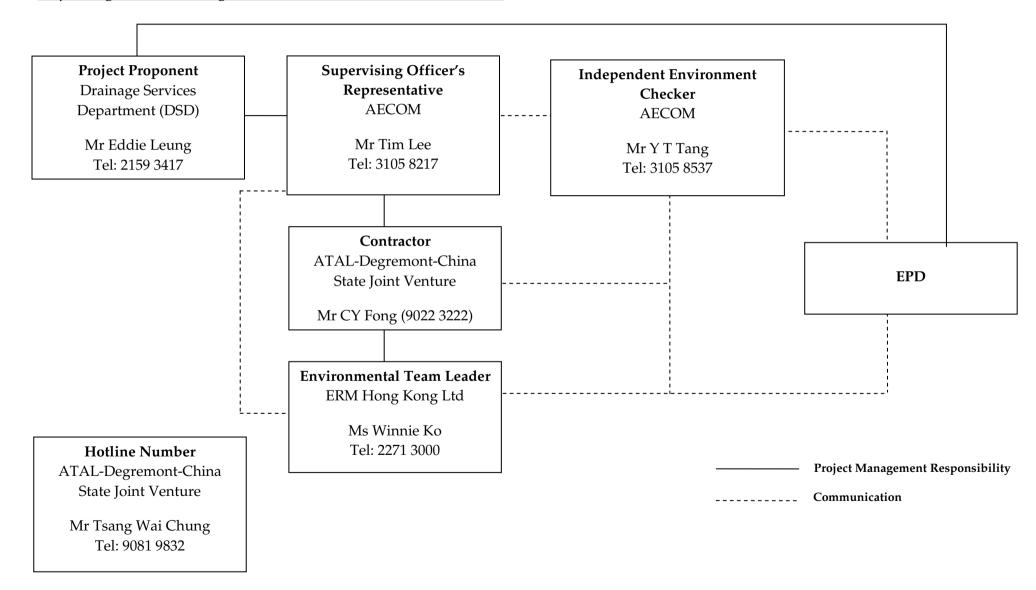

Annex D

Locations of Air Quality Monitoring Stations

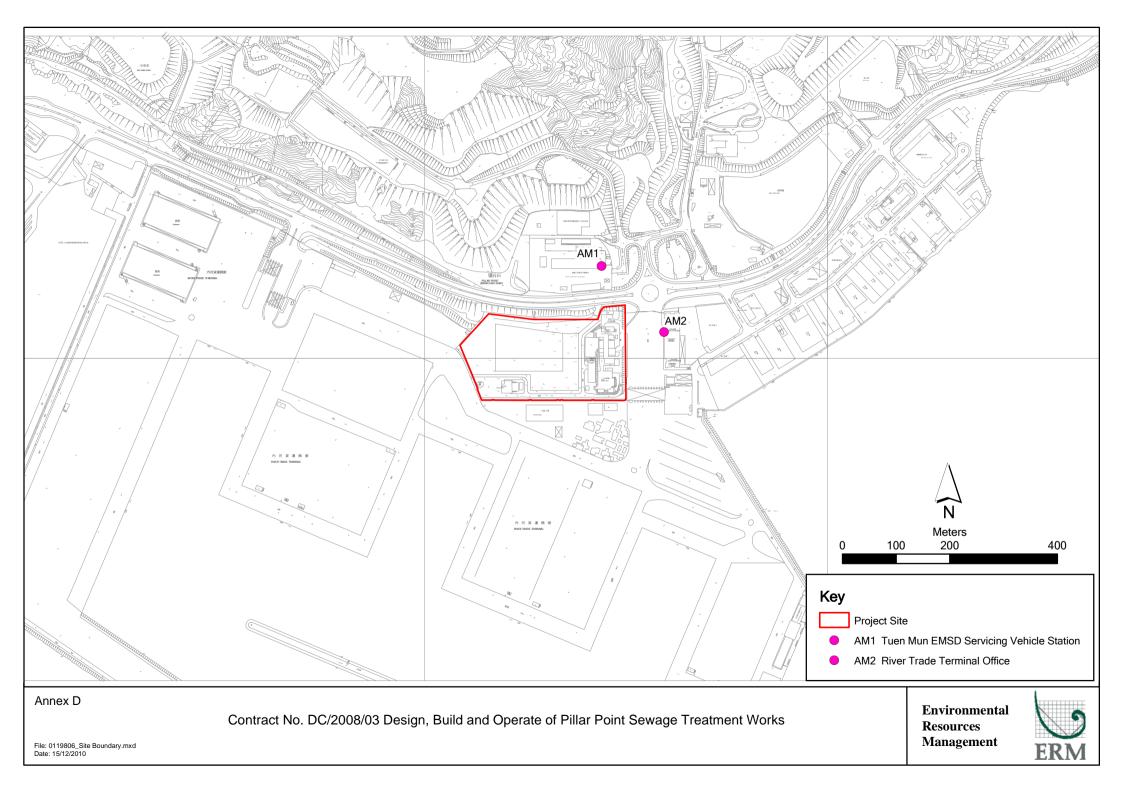



AM1 – Tuen Mun EMSD Servicing Vehicle Station



AM2 - River Trade Terminal Office

Annex E

Monitoring Schedule of Reporting Month and Next Month

#### Contract No. DC/2008/03 - Design, Build and Operate Pillar Point Sewage Treatment Works (Tuen Mun EMSD Servicing Vehicle Station - AM1 & River Trade Terminal Office - AM2) December 2011

| Sunday | Monday                | Tuesday               | Wednesday             | Thursday              | Friday                | Saturday |
|--------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|----------|
|        |                       |                       |                       | 01-Dec                | 02-Dec                | 03-Dec   |
|        |                       |                       |                       | 3X1-hr & 1X 24-hr TSP |                       |          |
| 04-Dec | 05-Dec                | 06-Dec                | 07-Dec                | 08-Dec                | 09-Dec                | 10-Dec   |
|        |                       |                       | 3X1-hr & 1X 24-hr TSP |                       |                       |          |
| 11-Dec | 12-Dec                | 13-Dec                | 14-Dec                | 15-Dec                | 16-Dec                | 17-Dec   |
|        |                       | 3X1-hr & 1X 24-hr TSP |                       |                       |                       |          |
| 18-Dec | 19-Dec                | 20-Dec                | 21-Dec                | 22-Dec                | 23-Dec                | 24-Dec   |
|        | 3X1-hr & 1X 24-hr TSP |                       |                       |                       | 3X1-hr & 1X 24-hr TSP |          |
| 25-Dec | 26-Dec                | 27-Dec                | 28-Dec                | 29-Dec                | 30-Dec                | 31-Dec   |
|        |                       |                       |                       | 3X1-hr & 1X 24-hr TSP |                       |          |

#### Contract No. DC/2008/03 - Design, Build and Operate Pillar Point Sewage Treatment Works (Tuen Mun EMSD Servicing Vehicle Station - AM1 & River Trade Terminal Office - AM2) January 2012

| Sunday | Monday                | Tuesday               | Wednesday             | Thursday              | Friday                | Saturday |
|--------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|----------|
| 01-Jan | 02-Jan                | 03-Jan                | 04-Jan                | 05-Jan                | 06-Jan                | 07-Jan   |
|        |                       |                       |                       | 3X1-hr & 1X 24-hr TSP |                       |          |
| 08-Jan | 09-Jan                | 10-Jan                | 11-Jan                | 12-Jan                | 13-Jan                | 14-Jan   |
|        |                       |                       | 3X1-hr & 1X 24-hr TSP |                       |                       |          |
| 15-Jan | 16-Jan                | 17-Jan                | 18-Jan                | 19-Jan                | 20-Jan                | 21-Jan   |
|        |                       | 3X1-hr & 1X 24-hr TSP |                       |                       |                       |          |
| 22-Jan | 23-Jan                | 24-Jan                | 25-Jan                | 26-Jan                | 27-Jan                | 28-Jan   |
|        | 3X1-hr & 1X 24-hr TSP |                       |                       |                       | 3X1-hr & 1X 24-hr TSP |          |
| 29-Jan | 30-Jan                | 31-Jan                |                       |                       |                       |          |
|        |                       |                       |                       |                       |                       |          |

Annex F

24-hour and 1-hour TSP Monitoring Results

#### 1-hour TSP Monitoring Results

Station AM1

\*

|           |       |        |         | TSP           |              |             |                               |             | Wind Speed |         |        |
|-----------|-------|--------|---------|---------------|--------------|-------------|-------------------------------|-------------|------------|---------|--------|
|           | Start | Finish | Weather | Concentration | Action Level | Limit Level | Site Conditions /             | Temperature | *          | Sampler | Filter |
| Date      | Time  | Time   |         | (µg/m³)       | (µg/m³)      | (µg/m³)     | <b>Observations / Remarks</b> | (℃)         | (m/s)      | ID      | ID     |
| 01-Dec-11 | 13:10 | 14:10  | Cloudy  | 100           | 343          | 500         | Construction work in progress | 19          | *          | 7580    | 3071   |
| 01-Dec-11 | 14:10 | 15:10  | Cloudy  | 93            | 343          | 500         | Construction work in progress | 19          | *          | 7580    | 3072   |
| 01-Dec-11 | 15:10 | 16:10  | Cloudy  | 97            | 343          | 500         | Construction work in progress | 19          | *          | 7580    | 3099   |
| 07-Dec-11 | 13:10 | 14:10  | Cloudy  | 143           | 343          | 500         | Construction work in progress | 24          | *          | 7580    | 3113   |
| 07-Dec-11 | 14:10 | 15:10  | Cloudy  | 185           | 343          | 500         | Construction work in progress | 24          | *          | 7580    | 3114   |
| 07-Dec-11 | 15:10 | 16:10  | Cloudy  | 145           | 343          | 500         | Construction work in progress | 25          | *          | 7580    | 3115   |
| 13-Dec-11 | 13:10 | 14:10  | Sunny   | 145           | 343          | 500         | Construction work in progress | 18.5        | *          | 7580    | 3183   |
| 13-Dec-11 | 14:10 | 15:10  | Sunny   | 132           | 343          | 500         | Construction work in progress | 19.5        | *          | 7580    | 3188   |
| 13-Dec-11 | 15:10 | 16:10  | Sunny   | 133           | 343          | 500         | Construction work in progress | 20          | *          | 7580    | 3189   |
| 19-Dec-11 | 13:10 | 14:10  | Sunny   | 117           | 343          | 500         | Construction work in progress | 17          | *          | 7580    | 3267   |
| 19-Dec-11 | 14:10 | 15:10  | Sunny   | 108           | 343          | 500         | Construction work in progress | 17.5        | *          | 7580    | 3268   |
| 19-Dec-11 | 15:10 | 16:10  | Sunny   | 117           | 343          | 500         | Construction work in progress | 18.5        | *          | 7580    | 3269   |
| 24-Dec-11 | 13:10 | 14:10  | Sunny   | 119           | 343          | 500         | Construction work in progress | 14          | *          | 7580    | 3284   |
| 24-Dec-11 | 14:10 | 15:10  | Sunny   | 119           | 343          | 500         | Construction work in progress | 14          | *          | 7580    | 3285   |
| 24-Dec-11 | 15:10 | 16:10  | Sunny   | 120           | 343          | 500         | Construction work in progress | 14.5        | *          | 7580    | 3286   |
| 30-Dec-11 | 13:10 | 14:10  | Sunny   | 140           | 343          | 500         | Construction work in progress | 17.5        | *          | 7580    | 3298   |
| 30-Dec-11 | 14:10 | 15:10  | Sunny   | 127           | 343          | 500         | Construction work in progress | 18          | *          | 7580    | 3240   |
| 30-Dec-11 | 15:10 | 16:10  | Sunny   | 143           | 343          | 500         | Construction work in progress | 18.5        | *          | 7580    | 3241   |
|           |       |        | Min.    | 93            |              |             |                               |             |            |         |        |
|           |       |        | Max.    | 185           | 1            |             |                               |             |            |         |        |

Max.185Average127

Wind Speed data is presented in the Meteorological Data table

#### 1-hour TSP Monitoring Results

Station AM2

\*

|           |       |        |         | TSP                  |                      |             |                               |             | Wind Speed |         |        |
|-----------|-------|--------|---------|----------------------|----------------------|-------------|-------------------------------|-------------|------------|---------|--------|
|           | Start | Finish | Weather | Concentration        | Action Level         | Limit Level | Site Conditions /             | Temperature | *          | Sampler | Filter |
| Date      | Time  | Time   |         | (µg/m <sup>3</sup> ) | (µg/m <sup>3</sup> ) | (µg/m³)     | <b>Observations / Remarks</b> | (°C)        | (m/s)      | ID      | ID     |
| 01-Dec-11 | 13:00 | 14:00  | Cloudy  | 108                  | 383                  | 500         | Construction work in progress | 19          | *          | 1252    | 3067   |
| 01-Dec-11 | 14:00 | 15:00  | Cloudy  | 112                  | 383                  | 500         | Construction work in progress | 19          | *          | 1252    | 3068   |
| 01-Dec-11 | 15:00 | 16:00  | Cloudy  | 119                  | 383                  | 500         | Construction work in progress | 19          | *          | 1252    | 3069   |
| 07-Dec-11 | 13:00 | 14:00  | Cloudy  | 159                  | 343                  | 500         | Construction work in progress | 24          | *          | 1252    | 3109   |
| 07-Dec-11 | 14:00 | 15:00  | Cloudy  | 167                  | 343                  | 500         | Construction work in progress | 24          | *          | 1252    | 3110   |
| 07-Dec-11 | 15:00 | 16:00  | Cloudy  | 168                  | 343                  | 500         | Construction work in progress | 25          | *          | 1252    | 3111   |
| 13-Dec-11 | 13:00 | 14:00  | Sunny   | 123                  | 383                  | 500         | Construction work in progress | 18.5        | *          | 1252    | 3187   |
| 13-Dec-11 | 14:00 | 15:00  | Sunny   | 123                  | 383                  | 500         | Construction work in progress | 19.5        | *          | 1252    | 3184   |
| 13-Dec-11 | 15:00 | 16:00  | Sunny   | 112                  | 383                  | 500         | Construction work in progress | 20          | *          | 1252    | 3185   |
| 19-Dec-11 | 13:00 | 14:00  | Sunny   | 165                  | 383                  | 500         | Construction work in progress | 17          | *          | 1252    | 3263   |
| 19-Dec-11 | 14:00 | 15:00  | Sunny   | 160                  | 383                  | 500         | Construction work in progress | 17.5        | *          | 1252    | 3264   |
| 19-Dec-11 | 15:00 | 16:00  | Sunny   | 156                  | 383                  | 500         | Construction work in progress | 18.5        | *          | 1252    | 3265   |
| 24-Dec-11 | 13:00 | 14:00  | Sunny   | 190                  | 383                  | 500         | Construction work in progress | 14          | *          | 1252    | 3280   |
| 24-Dec-11 | 14:00 | 15:00  | Sunny   | 184                  | 383                  | 500         | Construction work in progress | 14          | *          | 1252    | 3281   |
| 24-Dec-11 | 15:00 | 16:00  | Sunny   | 179                  | 383                  | 500         | Construction work in progress | 14.5        | *          | 1252    | 3282   |
| 30-Dec-11 | 13:00 | 14:00  | Sunny   | 140                  | 383                  | 500         | Construction work in progress | 17.5        | *          | 1252    | 3297   |
| 30-Dec-11 | 14:00 | 15:00  | Sunny   | 159                  | 383                  | 500         | Construction work in progress | 18          | *          | 1252    | 3237   |
| 30-Dec-11 | 15:00 | 16:00  | Sunny   | 168                  | 383                  | 500         | Construction work in progress | 18.5        | *          | 1252    | 3238   |
|           |       |        | Min.    | 108                  |                      |             |                               |             |            |         |        |

 Min.
 108

 Max.
 190

 Average
 150

Wind Speed data is presented in the Meteorological Data table

# Annex F - 24-hour and 1-hour TSP Monitoring Results

#### 24-hour TSP Monitoring Results

#### Station AM1

| Start     |       | Finis     | h     | Weather | Filter V | Veight (g) | Elapse<br>Read |          | Sampling<br>Time |         | / Rate (m | <sup>3</sup> /min) | TSP<br>Conc.         | Action<br>Level      | Limit<br>Level       | Observations / Remarks        | Sampler | Filter |
|-----------|-------|-----------|-------|---------|----------|------------|----------------|----------|------------------|---------|-----------|--------------------|----------------------|----------------------|----------------------|-------------------------------|---------|--------|
| Date      | Time  | Date      | Time  |         | Initial  | Final      | Initial        | Final    | (hrs)            | Initial | Final     | Average            | (µg/m <sup>3</sup> ) | (µg/m <sup>3</sup> ) | (µg/m <sup>3</sup> ) |                               | ID      | ID     |
| 01-Dec-12 | 16:10 | 02-Dec-12 | 16:10 | Cloudy  | 2.6916   | 2.8090     | 11981.18       | 12005.18 | 24.00            | 1.25    | 1.25      | 1.25               | 65                   | 183                  | 260                  | Construction work in progress | 7580    | 3100   |
| 07-Dec-12 | 16:10 | 08-Dec-12 | 16:10 | Cloudy  | 2.7133   | 2.8344     | 12008.18       | 12032.18 | 24.00            | 1.25    | 1.25      | 1.25               | 67                   | 183                  | 260                  | Construction work in progress | 7580    | 3116   |
| 13-Dec-12 | 16:10 | 14-Dec-12 | 16:10 | Sunny   | 2.7058   | 2.8339     | 12035.18       | 12059.18 | 24.00            | 1.25    | 1.25      | 1.25               | 71                   | 183                  | 260                  | Construction work in progress | 7580    | 3190   |
| 19-Dec-12 | 16:10 | 20-Dec-12 | 16:10 | Sunny   | 2.7695   | 2.8829     | 12062.18       | 12086.18 | 24.00            | 1.25    | 1.25      | 1.25               | 63                   | 183                  | 260                  | Construction work in progress | 7580    | 3270   |
| 24-Dec-12 | 16:10 | 25-Dec-12 | 16:10 | Sunny   | 2.7768   | 2.8990     | 12089.18       | 12113.18 | 24.00            | 1.25    | 1.25      | 1.25               | 68                   | 183                  | 260                  | Construction work in progress | 7580    | 3287   |
| 30-Dec-11 | 16:10 | 31-Dec-11 | 16:10 | Sunny   | 2.7737   | 2.9115     | 12116.18       | 12140.18 | 24.00            | 1.25    | 1.25      | 1.25               | 77                   | 183                  | 260                  | Construction work in progress | 7580    | 3242   |
|           |       |           |       |         |          |            |                |          |                  |         |           | Min.               | 63                   |                      |                      |                               |         |        |
|           |       |           |       |         |          |            |                |          |                  |         |           | Max.               | 77                   |                      |                      |                               |         |        |
|           |       |           |       |         |          |            |                |          |                  |         |           | Average            | 69                   |                      |                      |                               |         |        |

## 24-hour TSP Monitoring Results

#### Station AM2


| 0             |       | <b>F</b>       |           |         |         |                     | Elapse          |          | Sampling      |                 | <b>.</b>         | 3       | TSP                           | Action                        | Limit                         |                               |               |              |
|---------------|-------|----------------|-----------|---------|---------|---------------------|-----------------|----------|---------------|-----------------|------------------|---------|-------------------------------|-------------------------------|-------------------------------|-------------------------------|---------------|--------------|
| Start<br>Date | Time  | Finisł<br>Date | ו<br>Time | Weather | Initial | /eight (g)<br>Final | Read<br>Initial | Final    | Time<br>(hrs) | FIOW<br>Initial | Rate (m<br>Final | Average | Conc.<br>(µq/m <sup>3</sup> ) | Level<br>(µg/m <sup>3</sup> ) | Level<br>(µg/m <sup>3</sup> ) | Observations / Remarks        | Sampler<br>ID | Filter<br>ID |
| 01-Dec-12     | -     |                | -         | Cloudy  | 2.5996  | 2.7197              | 19998.20        | -        |               | 1.23            | 1.23             | 1.23    | (μg/m )<br>68                 | (µg/m)<br>192                 | (µg/m)<br>260                 | Construction work in progress |               | 3070         |
| 07-Dec-12     |       |                |           | Cloudy  | 2.7049  | 2.8421              | 20025.20        |          |               | 1.23            | 1.23             | 1.23    | 77                            | 192                           | 260                           | Construction work in progress |               | 3112         |
| 13-Dec-12     | 16:00 | 14-Dec-12      | 16:00     | Sunny   | 2.6649  | 2.7992              | 20052.20        | 20076.20 | 24.00         | 1.23            | 1.23             | 1.23    | 76                            | 192                           | 260                           | Construction work in progress | 1252          | 3186         |
| 19-Dec-12     | 16:00 | 20-Dec-12      | 16:00     | Sunny   | 2.7721  | 2.9122              | 20079.20        | 20103.20 | 24.00         | 1.23            | 1.23             | 1.23    | 79                            | 192                           | 260                           | Construction work in progress | 1252          | 3266         |
| 24-Dec-12     | 16:00 | 25-Dec-12      | 16:00     | Sunny   | 2.7360  | 2.8866              | 20106.20        | 20130.20 | 24.00         | 1.23            | 1.23             | 1.23    | 85                            | 192                           | 260                           | Construction work in progress | 1252          | 3283         |
| 30-Dec-11     | 16:00 | 31-Dec-11      | 16:00     | Sunny   | 2.7813  | 2.9201              | 20133.20        | 20157.20 | 24.00         | 1.23            | 1.23             | 1.23    | 78                            | 192                           | 260                           | Construction work in progress | 1252          | 3239         |

| 68 |
|----|
| 85 |
| 77 |
|    |


#### Meteorological Data Extracted from the Hong Kong Observatory

|            |         |                                    | Т                                 | uen Mun Station        |                              |                |
|------------|---------|------------------------------------|-----------------------------------|------------------------|------------------------------|----------------|
| Date       | Weather | Average Air<br>Temperature<br>(°C) | Average Relative<br>Humiditiy (%) | Total Rainfall<br>(mm) | Average Wind<br>Speed (km/h) | Wind Direction |
| 01-12-2011 | Cloudy  | 17.6                               | 57 - 86                           | 0.0                    | 10.5                         | N              |
| 02-12-2011 | Cloudy  | 14.7                               | 51 - 67                           | 0.0                    | 13.0                         | N              |
| 07-12-2011 | Cloudy  | 23.3                               | 69 - 88                           | 0.0                    | 7.0                          | N              |
| 08-12-2011 | Cloudy  | 19.2                               | 55 - 80                           | 0.0                    | 7.0                          | N              |
| 13-12-2011 | Sunny   | 17.3                               | 49 - 66                           | Trace                  | 10.5                         | N              |
| 14-12-2011 | Sunny   | 19.3                               | 60 - 68                           | 0.0                    | 8.5                          | N              |
| 19-12-2011 | Sunny   | 16.7                               | 58 - 84                           | 0.0                    | 9.0                          | N              |
| 20-12-2011 | Sunny   | 17.6                               | 57 - 86                           | Trace                  | 10.0                         | N              |
| 24-12-2011 | Sunny   | 5.5                                | 31 - 58                           | 0.0                    | 15.5                         | N              |
| 25-12-2011 | Sunny   | 13.5                               | 36 - 62                           | 0.0                    | 14.5                         | N              |
| 30-12-2011 | Sunny   | 18.7                               | 69 - 86                           | Trace                  | 10.0                         | N              |
| 31-12-2011 | Sunny   | 18.1                               | 64 - 95                           | 0.4                    | 7.5                          | N              |


1-hr TSP Levels for the Past 4 Months AM1 (Tuen Mun EMSD Vehicle Servicing Station)

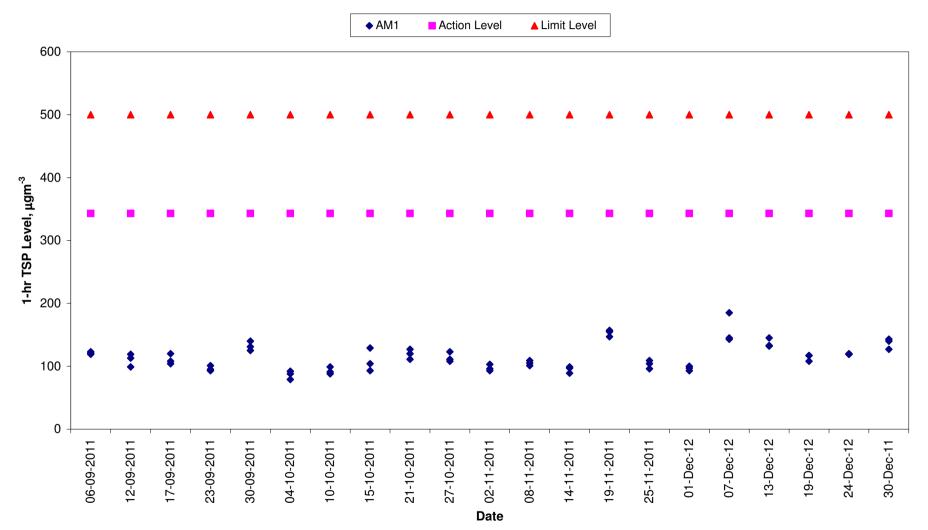


## 1-hr TSP Levels for the Past 4 Months AM2 (River Trade Terminal Office)

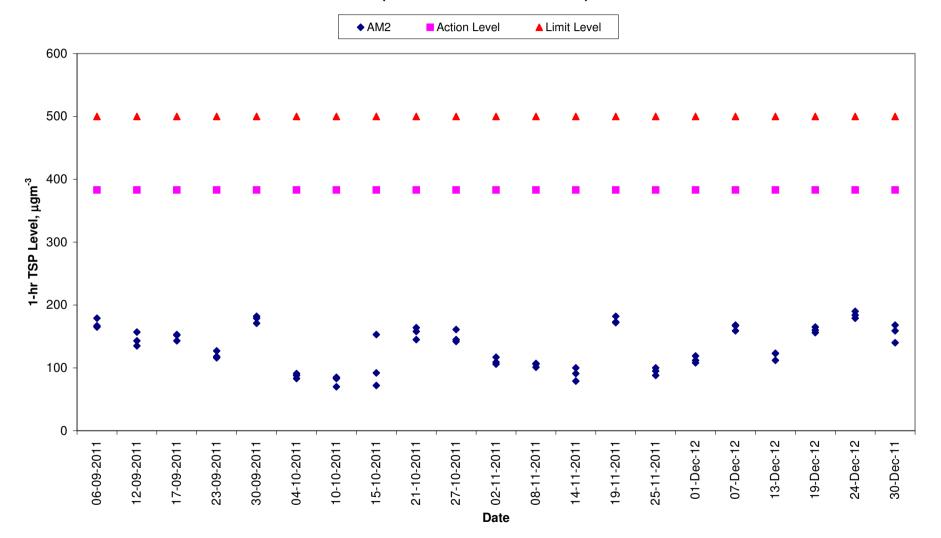

## 24-hr TSP Levels for the Past 4 Months AM1 (Tuen Mun EMSD Vehicle Servicing Station)

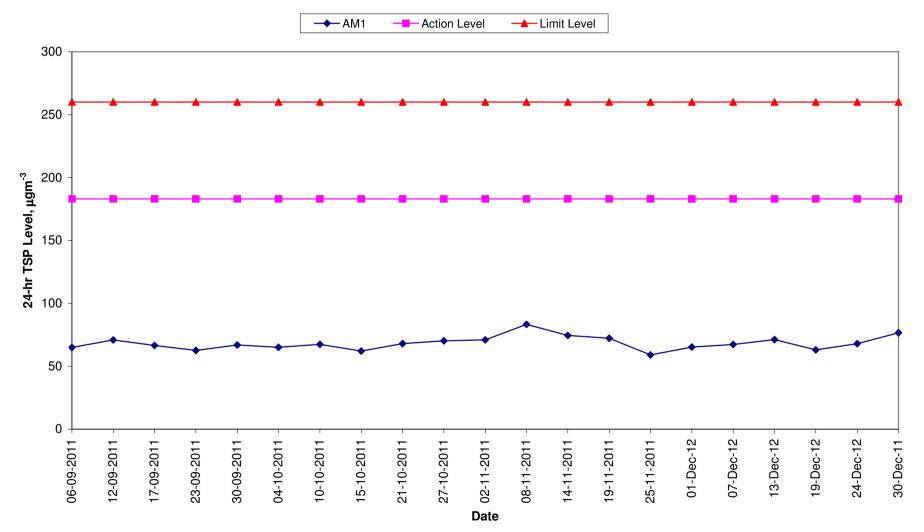

#### 24-hr TSP Levels for the Past 4 Months AM2 (River Trade Terminal Office)

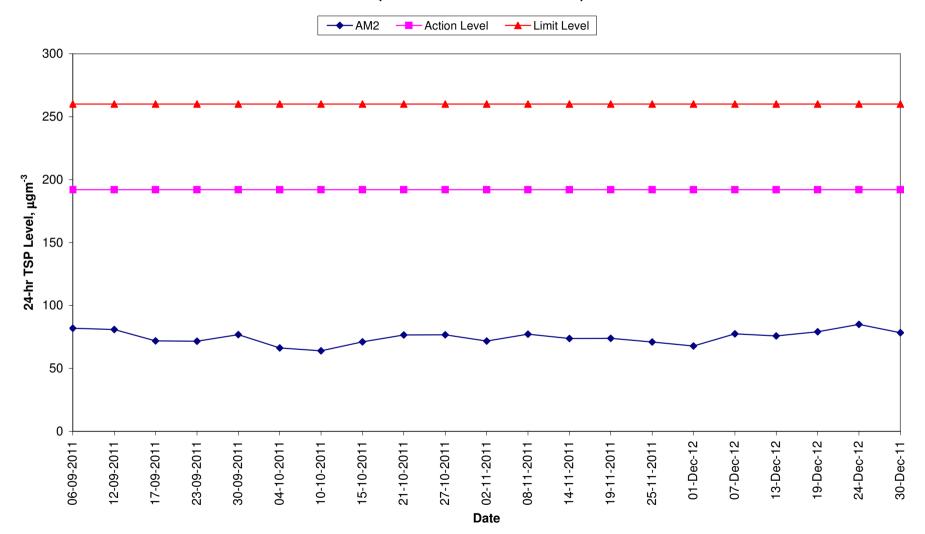

Annex G

Calibration Reports for HVSs

# TSP Monitoring Equipment

| Monitoring         | Location                                | Monitoring Equipment   |                      | Last Calibration Date | Next Calibration Date |
|--------------------|---|------------------------|----------------------|-----------------------|-----------------------|
| Station ID         |   |                        |                      |                       |                       |
| 24-hr and 1-hr TSF | )                                       | HVS                    | Calibrator           |                       |                       |
| AM1                | Tuen Mun EMSD Vehicle Servicing Station | GMW GS-2310 (S/N 7580) | CM-AIR-43 (S/N 1785) | 04 November 2011      | 04 January 2012       |
| AM2                | River Trade Terminal Office             | GMW GS-2310 (S/N 1252) | CM-AIR-43 (S/N 1785) | 04 November 2011      | 04 January 2012       |

#### High-Volume TSP Sampler 5-Point Calibration Record

| Location<br>Calibrated by<br>Date        | :<br>:<br>:      | EMSD<br>P.F.Yeung<br>14/11/2011 |
|--|------------------|---------------------------------|
| <u>Sampler</u><br>Model<br>Serial Number | :                | GMWS-2310 ACCU-VOL<br>S/N 7580  |
| Calibration Orfice and Stan              | dard Calibration | Relationship                    |
| Serial Number                            | :                | 1785                            |
| Service Date                             | :                | 25 May 2011                     |
| Slope (m)                                | :                | 2.00506                         |
| Intercept (b)                            | :                | -0.02062                        |
| Correlation Coefficient(r)               | :                | 0.99999                         |
| Standard Condition                       |                  |                                 |
| Pstd (hpa)                               | :                | 1013                            |
| Tstd (K)                                 | :                | 298.18                          |
| Calibration Condition                    |                  |                                 |
| Pa (hpa)                                 | :                | 1013                            |
| Ta(K)                                    | :                | 300                             |

| Resi | stance Plate | dH [green liquid]<br>(inch water) | Z     | X=Qstd<br>(cubic meter/min) | IC | Y    |
|------|--------------|-----------------------------------|-------|-----------------------------|----|------|
| 1    | 18 holes     | 11.3                              | 3.350 | 1.681                       | 52 | 51.8 |
| 2    | 13 holes     | 9.5                               | 3.072 | 1.542                       | 47 | 46.8 |
| 3    | 10 holes     | 7.1                               | 2.656 | 1.335                       | 41 | 40.9 |
| 4    | 7 holes      | 4.5                               | 2.114 | 1.065                       | 32 | 31.9 |
| 5    | 5 holes      | 2.6                               | 1.607 | 0.812                       | 24 | 23.9 |

Sampler Calibration Relationship

Slope(m):<u>31.928</u> Intercept(b):<u>-1.995</u>

Correlation Coefficient(r): 0.9997

Checked by: <u>Magnum Fan</u>

Date: 15/11/2011

# High-Volume TSP Sampler 5-Point Calibration Record

| Location<br>Calibrated by<br>Date | :<br>:<br>: | River Trade<br>K.T.Ho<br>14/11/2011 |
|-----------------------------------|-------------|-------------------------------------|
| <u>Sampler</u><br>Model           |             | GMWS-2310 ACCU-VOL                  |
| Serial Number                     | :           | S/N 1252                            |
| Calibration Orfice and Standard   | d Calibrat  | tion Relationship                   |
| Serial Number                     | :           | 1785                                |
| Service Date                      | :           | 25 May 2011                         |
| Slope (m)                         | :           | 2.00506                             |
| Intercept (b)                     | :           | -0.02062                            |
| Correlation Coefficient(r)        | :           | 0.99999                             |
| Standard Condition                |             |                                     |
| Pstd (hpa)                        | :           | 1013                                |
| Tstd (K)                          | :           | 298.18                              |
| Calibration Condition             |             |                                     |

| Calibration Condition |   |      |
|-----------------------|---|------|
| Pa (hpa)              | : | 1013 |
| Ta(K)                 | : | 300  |
|                       |   |      |

| Resi | istance Plate | dH [green liquid] | Z     | X=Qstd            | IC | Y    |
|------|---------------|-------------------|-------|-------------------|----|------|
|      |               | (inch water)      |       | (cubic meter/min) |    |      |
| 1    | 18 holes      | 11.2              | 3.335 | 1.674             | 64 | 63.8 |
| 2    | 13 holes      | 9.1               | 3.007 | 1.510             | 56 | 55.8 |
| 3    | 10 holes      | 7.3               | 2.693 | 1.353             | 48 | 47.8 |
| 4    | 7 holes       | 4.6               | 2.138 | 1.076             | 35 | 34.9 |
| 5    | 5 holes       | 2.6               | 1.607 | 0.812             | 22 | 21.9 |

Sampler Calibration Relationship

 $Slope(m): \underline{48.454} \quad Intercept(b): \underline{-17.414} \quad Correlation \ Coefficient(r): \underline{0.9999}$ 

Checked by: <u>Magnum Fan</u> Date: <u>15/011/2011</u>

Annex H

Event/Action Plan for Air Quality Monitoring

| Action Level/Limit<br>Level                          | Environmental Team Leader (ETL)  | Independent Environmental<br>Checker (IEC)   | Supervising Officer<br>Representative (SOR)   | Contractor   |
|--|--|--|---|--|
| Action Level   |  |  |   |  |
| Exceedance for one sample                            | <ul> <li>Identify source, investigate the causes of complaint and propose remedial measures;</li> <li>Inform IEC and SOR;</li> <li>Repeat measurement to confirm findings;</li> <li>Increase monitoring frequency to daily.</li> </ul>   | <ul> <li>Check monitoring data submitted<br/>by ET;</li> <li>Check Contractor's working<br/>method.</li> </ul>   | • Notify Contractor and DSD.  | <ul> <li>Rectify any unacceptable practice;</li> <li>Amend working methods if appropriate.</li> </ul>  |
| Exceedance for two or<br>more consecutive<br>samples | <ul> <li>Identify source;</li> <li>Inform IEC and SOR;</li> <li>Advise the SOR on the effectiveness of the proposed remedial measures;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Discuss with IEC and Contractor on remedial actions required;</li> <li>If exceedance continues, arrange meeting with IEC and SOR;</li> <li>If exceedance stops, cease additional monitoring.</li> </ul> | <ul> <li>Check monitoring data submitted<br/>by ET;</li> <li>Check Contractor's working<br/>method;</li> <li>Discuss with ET and Contractor<br/>on possible remedial measures;</li> <li>Advise the ET on the effectiveness<br/>of the proposed remedial<br/>measures;</li> <li>Supervise Implementation of<br/>remedial measures.</li> </ul> | <ul> <li>Confirm receipt of notification<br/>of exceedance in writing;</li> <li>Notify Contractor and DSD;</li> <li>Ensure remedial measures<br/>properly implemented.</li> </ul> | <ul> <li>Submit proposals for remedial actions to IEC within three working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> </ul> |

## Table H1Event Action Plan for Air Quality Monitoring

#### ENVIRONMENTAL RESOURCES MANAGEMENT

| Action Level/Limit<br>Level                          | Environmental Team Leader (ETL)   | Independent Environmental<br>Checker (IEC)  | Supervising Officer<br>Representative (SOR)   | Contractor  |
|--|---|---|---|---|
| Limit Level  |   |   |   |   |
| Exceedance for one<br>sample                         | <ul> <li>Identify source, investigate the causes of exceedance and propose remedial measures;</li> <li>Inform IEC, SOR, DSD and EPD;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD, DSD and SOR informed of the results.</li> </ul>   | on possible remedial measures;  | <ul> <li>Confirm receipt of notification<br/>of exceedance in writing;</li> <li>Notify Contractor;</li> <li>Ensure remedial measures<br/>properly implemented.</li> </ul>   | <ul> <li>Take immediate action to avoid<br/>further exceedance; Submit<br/>proposals for remedial actions to<br/>IEC within three working days of<br/>notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> </ul>   |
| Exceedance for two or<br>more consecutive<br>samples | <ul> <li>Notify IEC, SOR, DSD and EPD;</li> <li>Identify source;</li> <li>Repeat measurement to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Arrange meeting with IEC and SOR to discuss the remedial actions to be taken;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD, DSD and SOR informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> </ul> | <ul> <li>Discuss amongst SOR, ET, and<br/>Contractor on the potential<br/>remedial actions;</li> <li>Review Contractor's remedial<br/>actions whenever necessary to<br/>assure their effectiveness and<br/>advise the SOR accordingly;</li> <li>Supervise the implementation of<br/>remedial measures.</li> </ul> | <ul> <li>Confirm receipt of notification of exceedance in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Ensure remedial measures properly implemented;</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ul> | <ul> <li>Take immediate action to avoid<br/>further exceedance;</li> <li>Submit proposals for remedial<br/>actions to IEC within three<br/>working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem<br/>still not under control;</li> <li>Stop the relevant portion of works<br/>as determined by the SOR until<br/>the exceedance is abated.</li> </ul> |

#### ENVIRONMENTAL RESOURCES MANAGEMENT

Annex I

Implementation Schedule of Mitigation Measures

# Annex I Summary of Mitigation Measures Implementation Schedule

| Type of<br>Impact | Environmental Protection Measures  | Location/ Timing                         | Status   |
|-------------------|--|--|--|
| Summary of Envi   | ronmental Mitigation Measures in the EIA and EM&A Manual   | •  |  |
| Construction Pha  | se   |  |  |
| Air Quality       | Dust mitigation measures stipulated in <i>the Air Pollution Control</i><br>( <i>Construction Dust</i> ) <i>Regulation</i> shall be incorporated to control Post<br>emission. Notice shall be given to authority prior to commencing of<br>work.  | Work sites / during construction period  | $\Delta$ . Notice of works commencement was submitted to EPD on 3 August 2010. |
| Water Quality     | The practices outlined in ProPECC PN 1/94 Construction Site Drainage<br>should be adopted. It is recommended to install perimeter channels in<br>the works areas to intercept runoff as site boundary prior to the<br>commencement of any earthwork. To prevent storm runoff from<br>washing across exposed soil surfaces, intercepting channels should be<br>provided. Drainage channels are also required to convey site runoff to<br>sand/silt traps and oil interceptors. Provision of regular cleaning and<br>maintenance can ensure the normal operation of these facilities<br>throughout the construction period. Any practical options for the<br>diversion and re-alignment of drainage should comply with both<br>engineering and environmental requirements in order to ensure<br>adequate hydraulic capacity of all drains.                                 | Work site/During the construction period |  |
| Water Quality     | There is a need to apply to EPD for a discharge license under the WPCO for discharging effluent from the construction site. The discharge quality is required to meet the requirements specified in the discharge license. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Reuse and recycling of the treated effluent can minimize water consumption and reduce the effluent discharge volume. The beneficial uses of the treated effluent may include dust suppression, wheel washing and general cleaning. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD. | Work site/During the construction period | Δ. Discharge licence was awarded by EPD<br>on 7 December 2010.                 |
| Water Quality     | The construction programme should be properly planned to minimize soil excavation, if any, in rainy seasons. This prevents soil erosion from   | Work site/During the construction period | Δ  |

| Type of<br>Impact   | Environmental Protection Measures  | Location/ Timing                         | Status       |
|---------------------|--|--|--------------|
|                     | exposed soil surfaces. Any exposed soil surfaces should also be<br>properly protected to minimize dust emission. In areas where a large<br>amount of exposed soil exists, earth bunds or sand bags should be<br>provided. Exposed stockpiles should be covered with tarpaulin or<br>impervious sheets at all times. The stockpiles of materials should be<br>placed at locations away from any stream course so as to avoid releasing<br>materials into the water bodies. Final surfaces of earthworks should be<br>compacted and protected by permanent work. It is suggested that haul<br>roads should be paved with concrete and the temporary access roads<br>protected using crashed stone or gravel, wherever practicable. Wheel<br>washing facilities should be provided at all site exists to ensure that<br>earth, mud and debris would not be carried out of the works areas by<br>vehicles. |  |              |
| Water Quality       | Good sites practices should be adopted to clean the rubbish and litter on<br>the construction sites so as to prevent the rubbish and litter from<br>spreading from the site area. It is recommended to clean the<br>construction sites on a regular basis.   | Work site/During the construction period | Δ            |
| Water Quality       | The presence of construction workers generates sewage. It is<br>recommended to provide sufficient chemical toilets in the works areas.<br>The toilet facilities should be more than 30m from any watercourse. A<br>licensed water collector should be deployed to clean the chemical toilets<br>on a regular basis. The construction workers can also make use of the<br>existing toilet facilities within the PPSTW as necessary.   | Work site/During the construction period | N            |
| Water Quality       | Notices should be posted at conspicuous locations to remind the<br>workers not to discharge any sewage or wastewater into the nearby<br>environment during the construction phase of the project. Regular<br>environmental audit on the construction phase of the project. Regular<br>environmental audit on the construction site can provide an effective<br>control of any malpractices and can achieve continual improvement of<br>environmental performance on site.  | Work site/During the construction period |              |
| Waste<br>Management | Contractor must register as a chemical waste producer if chemical<br>wastes would be produced from the construction activities. The Waste<br>Disposal Ordinance (Cap 354) and its subsidiary regulations in  | Work site/During the construction period | $\checkmark$ |

| Type of<br>Impact   | Environmental Protection Measures   | Location/ Timing                         | Status       |
|---------------------|---|--|--------------|
|                     | particular the Waste Disposal (Chemical Waste) (General) Regulation<br>should be observed and complied with for control of chemical wastes.   |  |              |
| Waste<br>Management | Any service shop and maintenance facilities should be located on hard<br>standings within a bunded area, and stumps and oil interceptors should<br>be provided. Maintenance of vehicles and equipment involving<br>activities with potential for leakage and spillage should only be<br>undertaken within the areas appropriately equipped to control these<br>discharges.        | Work site/During the construction period | √            |
| Waste<br>Management | Disposal of chemical wastes should be carried out in compliance with<br>the Waste Disposal Ordinance. The Code of Practice on the Packaging,<br>Labelling and Storage of Chemical Wastes published under the Waste<br>Disposal Ordinance details the requirements to deal with the chemical<br>wastes. General requirements are given as follows:                                 | Work site/During the construction period | $\checkmark$ |
|                     | <ul> <li>Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport.</li> <li>Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents.</li> <li>Storage area should be selected at a safe location on site and</li> </ul> |  |              |
|                     | • Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.  |  |              |
| Waste<br>Management | <i>Good Site Practices</i> Recommendations for good site practices during the construction activities include:  | Work site/During the construction period | <>           |
|                     | • Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site   |  |              |
|                     | • Training of site personnel in proper waste management and chemical handling procedures  |  |              |
|                     | Provision of sufficient waste disposal points and regular collection     of waste   |  |              |
|                     | • Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by   |  |              |

| Type of<br>Impact   | Environmental Protection Measures  | Location/ Timing  | Status       |
|---------------------|--|---|--------------|
|                     | <ul> <li>transporting wastes in enclosed containers</li> <li>Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.</li> <li>Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility.</li> </ul>   |   |              |
| Waste<br>Management | <ul> <li>Waste Reduction Measures</li> <li>Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</li> <li>Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> <li>Encourage collection of aluminium cans by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force</li> <li>Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> <li>Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> </ul> | Work site/During planning & design stage, and<br>construction stage | $\checkmark$ |
| Waste<br>Management | <i>General Refuse</i><br>General refuse should be stored in enclosed bins or compaction units<br>separate from C&D material. A reputable waste collector should be<br>employed by the contractor to remove general refuse from the site,<br>separately from C&D material. Preferably an enclosed and covered area<br>should be provided to reduce the occurrence of 'wind blown' light<br>material.  | Work site / During the construction period                          | <>           |
| Waste<br>Management | Construction and Demolition Material<br>In order to minimise the impact resulting from collection and  | Work site / During design stage & construction period               | $\checkmark$ |

| Type of<br>Impact   | Environmental Protection Measures   | Location/ Timing                                      | Status       |
|---------------------|---|---|--------------|
|                     | transportation of C&D material for off-site disposal, the excavated<br>material generated from site formation works for the proposed new<br>facilities and units at the STW should be reused on-site as far as<br>practicable. The surplus excavated material should be disposed of at the<br>designated public fill reception facility, as agreed with the Secretary of<br>the Public Fill Committee, for other beneficial uses. |   |              |
| Waste<br>Management | <ul> <li>Mitigation measures and good site practices should be followed to control potential environmental impact from handling and transportation of C&amp;D material. The mitigation measures include:</li> <li>Where it is unavoidable to have transient stockpiles of C&amp;D material pending collection for disposal, the transient stockpiles shall be located away from waterfront or storm drains as far as</li> </ul>   | Work site / During design stage & construction period | $\checkmark$ |
|                     | <ul> <li>possible.</li> <li>Open stockpiles of construction materials or construction wastes on-<br/>site should be covered with tarpaulin or similar fabric.</li> <li>Skip hoist for material transport should be totally enclosed by<br/>impervious sheeting.</li> </ul>  |   |              |
|                     | <ul> <li>Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site</li> <li>The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.</li> </ul>  |   |              |
|                     | <ul> <li>The load of dusty materials carried by vehicle leaving a construction<br/>site should be covered entirely by clean impervious sheeting to<br/>ensure dust materials do not leak from the vehicle.</li> </ul>   |   |              |
|                     | • All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet.   |   |              |
|                     | • The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading.  |   |              |
| Waste<br>Management | When disposing C&D material at a public filling facility, it shall be noted that the material shall only consist of earth, building debris and broken rock and concrete. The material shall be free from marine mud,  | Work site/During design stage & construction period   | $\checkmark$ |

| Type of<br>Impact     | Environmental Protection Measures  | Location/ Timing                                       | Status   |
|-----------------------|--|--|--|
| Waste<br>Management   | <ul> <li>household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered to be unsuitable by the Filling Supervisor. In order to monitor the disposal of the surplus C&amp;D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work with reference to the ETWB TCW No. 31/2004 "Trip Ticket System for Disposal of Construction and Demolition Materials" as attached in Appendix 7-1. An Independent Environmental Checker should be responsible for auditing the results of the system.</li> <li><i>Chemical Waste</i></li> <li>If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste</li> <li>Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical waste should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.</li> </ul> | Work site / During the construction period             |  |
| Landscape &<br>Visual | Temporary Tree NurseriesTemporary tree nurseries may be set up for the transplanted tree and<br>proposed trees at an early stage to allow small trees to grow during the<br>construction periods. By the time when planting area becomes available,<br>trees mature and increase in trunk & spread size. They will require<br>minimal pruning and suffer much less damage during transplanting<br>when comparing the travel distance from an on-site nursery to an off-site<br>nursery.  | Work site/During design stage & construction<br>period | √. A tree nursery has been set up off-site near the site office. |

| Type of<br>Impact     | Environmental Protection Measures  | Location/ Timing                                       | Status       |
|-----------------------|--|--|--------------|
|                       | Besides, these trees may also be positioned as visual mitigation during the construction period.   |  |              |
| Landscape &<br>Visual | No-intrusion Zone<br>To maximize protection to existing trees and ground vegetation,<br>construction contracts may designate "No-intrusion Zone" to various<br>areas within the site boundary with rigid and durable fencing for each<br>individual no-intrusion zone. The contractor should close monitor and<br>restrict the site working staff not to enter the "no-intrusion zone", even<br>for non-direct construction activities and storage of equipment.   | Work site/During design stage & construction period    | <>           |
| Landscape &<br>Visual | Hoarding<br>Hoarding or boundary fencing for construction shall be considered. It<br>should be sensitively designed, subtle, camouflaged and more<br>'permeable' so that they fit into the existing environment when looking<br>from outside.  | Work site/During design stage & construction period    | $\checkmark$ |
| Landscape &<br>Visual | Dust and Erosion Control for Exposed Soil<br>Excavation works and demolition of existing building blocks and which<br>will be highly visible form surrounding areas should be well planned<br>and with precautions to suppress dust. Exposed soil shall be covered or<br>'camouflaged' and watered often. Areas that are expected to be left with<br>bare soil for a long period of time after excavation shall be properly<br>covered with suitable protective fabric. Silt and erosion shall be<br>controlled by ground barriers around the slope cutting area | Work site/During design stage & construction<br>period | \$           |
| Landscape &<br>Visual | Existing Tree Record Inventory         All retained trees should be record photographically at the commencement of the Contract, and carefully protected during the construction period. Detailed tree protection specification shall be allowed and included in the Contract Specification, which specifying the  | Work site/During design stage & construction period    | <>           |

| Type of<br>Impact     | Environmental Protection Measures  | Location/ Timing   | Status                                       |
|-----------------------|--|--|--|
|                       | tree protection requirement, submission and approval system, and the tree monitoring system.   |  |  |
| Landscape &<br>Visual | Construction LightAll security floodlights for construction sites shall be equipped with<br>adjustable shield, frosted diffusers and reflective covers, and be carefully<br>controlled to minimize light pollution and night-time glare to nearby<br>residences and GIC users. The Contractor shall consider other security<br>measures which shall minimize the visual impacts.   | Work site / During design stage & construction period    | V  |
| Landscape &<br>Visual | <u>Tree Transplanting</u><br>Apart from the 18 numbers of <i>"Leucaena leucocephala"</i> , which are<br>proposed to be felled in accordance with ETWB TCW No. 3/2006, all the<br>affected trees shall be transplanted. Where practicable, trees shall be<br>directly transplanted to permanent on-site locations. The location of the<br>transplanted tree is shown in <b>Figure 8.9.1</b> .   | Work site / During design stage & construction period    | $\Delta$ . Tree transplantation in progress. |
| Landscape &<br>Visual | Tree Compensation RatioThe total number of compensatory trees planted in the project area shall<br>not be less than 1:1 ratios by new trees. Required numbers and locations<br>of compensatory trees shall be determined and agreed with Government<br>during the tree felling application process under ETWCTC 3/2006.<br>Compensatory trees shall be at least heavy standard size to create<br>"immediate" greening effect. 81 numbers of "Cassia surattensis" will be<br>provided as the additional compensatory planting for loss of greenery in<br>the area due to removal of the affected trees. The location of the<br>additional compensatory planting is shown in Figure 8.9.1. | Work site / During design stage & construction<br>period | N/A  |
| Landscape &<br>Visual | Re-use of Existing Soil and Advance formation of Planting AreaExisting topsoil shall be re-used where possible for new planting areaswithin the project. Advance formation of planting area and earlyimplementation of the plating works can minimize adverse impact ontrees. The construction program shall consider using the soil removed   | Work site / During design stage & construction period    | $\checkmark$                                 |

| Type of<br>Impact        | Environmental Protection Measures   | Location/ Timing                                      | Status   |
|--------------------------|---|---|--|
|                          | from one phase for backfilling another. Suitable storage ground, gathering ground and mixing ground may be set up on-site as necessary.   |   |  |
| Landscape &<br>Visual    | Establishment Period<br>12 month establishment period for the soft landscape works will be<br>allowed in the main contract. Most construction contracts in Hong Kong<br>require the Contractor to carry out routine horticultural operations,<br>including watering, pruning, weeding, pest control, replacement of dead<br>plants etc. to ensure healthy establishment of new planting during a 12<br>month establishment period. This period also serves as a kind of<br>warranty / guarantee on the quality of the plants supplied and installed<br>by the Contractor. Monthly monitoring during the first year of<br>establishment period is recommended. | Work site/During operation period                     | N/A. To be implemented during<br>operation phase of Project. |
| Landscape &<br>Visual    | Re-instatement of excavated Area         All excavated area and disturbed area for utilities diversion, temporary road diversion, and pipeline woks will be reinstated to former conditions, subject to applicable Government Standards.  | Work site / During design stage & operation period    | N/A. To be implemented during operation phase of Project.    |
| Landscape &<br>Visual    | Appearance and Greening for the proposed structures<br>Compatible design, construction materials and surface finishes of the<br>proposed structure should match with the nearby existing external<br>appearance of PPSTW buildings for achieving visual uniformity.<br>Finishing materials shall have due consideration to form, basic color,<br>color/tone variation, micro-and macro-texture, and reflectivity/light<br>absorbance to avoid glare. Planting, such as turf, low groundcovers and<br>climbers, may also be planted on top of these elements to provide<br>greening and aesthetic effect.  | Work site / During design stage & operation<br>period | N/A. To be implemented during<br>operation phase of Project. |
| Summary of Key           | Environmental Mitigation Measures in Contract Requirements  |   | 1  |
| Air Quality              | Only Ultra-low-sulphur diesel (ULSD) should be used for all diesel-<br>operated plants and equipments on site   | Work sites / during construction period               | V  |
| Air Quality<br>and Noise | Plants and equipments of good operation conditions should be used on site.  | Work sites / during construction period               | $\checkmark$   |
| Noise                    | No diesel hammers should be used for piling works   | Work sites / during construction period               | $\checkmark$   |

| Type of<br>Impact       | Environmental Protection Measures  | Location/ Timing                        | Status       |
|-------------------------|--|---|--------------|
| Noise                   | Construction Noise Permits (CNP) should be applied for works conducted outside non-restricted hours.   | Work sites / during construction period | $\checkmark$ |
| Noise                   | Quiet construction equipments and the quietest practicable working<br>methodologies should be adopted for works whenever feasible. Noise<br>labels should be provided for air compressors. Hoods and cover panels<br>of generators and air compressors should be closed during operation.<br>Noise labels should be provided for air compressors and hand-held<br>percussive breakers. | Work sites / during construction period | $\checkmark$ |
| Waste<br>Management     | Temporary works construction on site should minimize the use of timber to reduce the quantity of C&D waste generated during works period.  | Work sites / during construction period | $\checkmark$ |
| Landscape and<br>Visual | Retained or to-be-transplanted trees on site should be properly protected<br>from physical damages and soil compacts with temporary fencing or<br>hessian armouring whenever feasible.   | Work sites / during construction period | $\diamond$   |

Remark:

- $\sqrt{}$  Compliance of Mitigation Measures
- <> Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- Non-compliance of Mitigation Measures but rectified by ATAL-Degrémont-China State JV
- Δ Deficiency of Mitigation Measures but rectified by ATAL-Degrémont-China State JV
- N/A Not Applicable in Reporting Period

Annex J

Waste Flow Table

## Contract No. : DC/2008/03 - Design, Build and Operate Pillar Point Sewage Treatment Works

### Monthly Summary Waste Flow Table

|           | Ac                          | ctual Quantities of In     | ert C&D Materials         | (Public Fill) Generat       | ed                         | Actu                   | al Quantities of Non-i                        | nert C&D Materials       | (Construction Waste | e) Generated                                |
|-----------|-----------------------------|----------------------------|---------------------------|-----------------------------|----------------------------|------------------------|---|--------------------------|---------------------|---|
| Month     | Total Quantity<br>Generated | Rocks & Broken<br>Concrete | Reused in the<br>Contract | Reused in other<br>Projects | Disposed as Public<br>Fill | Metals (see<br>Note 1) | Paper/ cardboard<br>packaging (see<br>Note 1) | Plastics<br>(see Note 2) | Chemical Waste      | Others, e.g. general<br>refuse (see Note 3) |
|           | tonne                       | tonne                      | tonne                     | tonne                       | tonne                      | kilogram               | kilogram                                      | kilogram                 | Litre               | tonne                                       |
| Nov 2010  | 2,248                       | 0                          | 0                         | 0                           | 2,248                      | 60                     | 100   | 0                        | 0                   | 18.05 (see Note 4)                          |
| Dec 2010  | 11,314 (see Note 4)         | 0                          | 0                         | 0                           | 11,314                     | 100                    | 120   | 20                       | 0                   | 28.4 (see Note 4)                           |
| Jan 2011  | 58,383 (see Note 4)         | 0                          | 0                         | 0                           | 58,383                     | 250                    | 280   | 60                       | 0                   | 4.59 (see Note 4)                           |
| Sub-total | 71,945                      | 0                          | 0                         | 0                           | 71,945                     | 410                    | 500   | 80                       | 0                   | 51.04                                       |
| Feb 2011  | 12,855                      | 0                          | 0                         | 0                           | 12,855                     | 100                    | 150   | 50                       | 0                   | 2.43 (see Note 4)                           |
| Mar 2011  | 22,859                      | 0                          | 0                         | 0                           | 22,859                     | 150                    | 180   | 55                       | 0                   | 9.02  |
| Apr 2011  | 8,547 (see Note 7)          | 0                          | 0                         | 5,684(see Note 5, 7)        | 2,863 (see Note 7)         | 50                     | 30  | 15                       | 0                   | 5.78  |
| Sub-total | 44,261                      | 0                          | 0                         | 5,684                       | 38,577                     | 300                    | 360   | 120                      | 0                   | 17.23                                       |
| May 2011  | 6,293 (see Note 7)          | 0                          | 0                         | 11 (see Note 5, 7)          | 6,282 (see Note 7)         | 45                     | 25  | 10                       | 360 (see Note 7)    | 8.83  |
| Jun 2011  | 4,587 (see Note 7)          | 0                          | 0                         | 0 (see Note 7)              | 4,587 (see Note 7)         | 40                     | 30  | 15                       | 0                   | 7.10  |
| Jul 2011  | 523                         | 0                          | 0                         | 0                           | 523                        | 15                     | 5   | 10                       | 0                   | 7.20  |
| Sub-total | 11,403                      | 0                          | 0                         | 11                          | 11,392                     | 100                    | 60  | 35                       | 360                 | 23.13                                       |
| Aug 2011  | 571 (see Note 11)           | 0                          | 0                         | 0                           | 571 (see Note 11)          | 0                      | 0   | 15                       | 450 (see Note 8)    | 6.12  |
| Sept 2011 | 235                         | 0                          | 0                         | 0                           | 235                        | 20                     | 0   | 0                        | 0                   | 12.15 (see Note 9)                          |
| Oct 2011  | 5,705 (see Note 10)         | 0                          | 0                         | 0                           | 5,705 (see Note 10)        | 100                    | 0   | 0                        | 0                   | 2.98  |
| Sub-total | 6,511                       | 0                          | 0                         | 0                           | 6,511                      | 120                    | 0   | 15                       | 450                 | 21.25                                       |
| Nov 2011  | 6,294                       | 0                          | 0                         | 0                           | 6,294                      | 50                     | 0   | 0                        | 0                   | 44.84                                       |
| Dec 2011  | 3,011                       | 0                          | 0                         | 0                           | 3,011                      | 20                     | 0   | 0                        | 0                   | 17.14                                       |
| Total     | 143,425                     | 0                          | 0                         | 5,695                       | 137,730                    | 1,000                  | 920   | 250                      | 810                 | 174.63                                      |

Notes: (1) Metal and paper/cardboard packaging were collected by recycler for recycling.

(2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material collected by recycler for recycling.

(3) General refuse was disposed of at WENT by subcontractors.

- (4) The waste flow data for November and December 2010, January and February 2011 was updated in March 2011based on SOR's comments and has been confirmed by the Contractor.
- (5) The inert C&D materials were reused in the Contract No. EP/SP/58/08 at Tuen Mun Tsang Tsui.
- (6) Chemical waste was collected though the licensed chemical waste collector, Dunwell Ind. (Holdings) Ltd, with the waste collection licence number 7111-757-W0015-WC.
- (7) The waste flow data for April, May and June 2011 was updated in August 2011 based on SOR's comments and has been confirmed by the Contractor.
- (8) The waste flow data of chemical waste for August 2011 was updated in October 2011 based on Contractor's revised waste flow summary.
- (9) The waste flow data of general refuse for September 2011 was updated in November 2011 based on Contractor's revised waste flow summary.
- (10) The waste flow data of C&D material for October 2011 was updated in December 2011 based on Contractor's revised waste flow summary.
- (11) The waste flow data of C&D material for August 2011 was updated in January 2011 based on SOR's comments and has been confirmed by the Contractor.

Annex K

Environmental Complaint, Environmental Summon and Presecution Log

| <b>Reporting Month</b> | Number of Complaints in Reporting Month | Number of Summons/Prosecutions in Reporting Month |
|------------------------|---|---|
| November 2010          | 0                                       | 0   |
| December 2010          | 0                                       | 0   |
| January 2011           | 0                                       | 0   |
| February 2011          | 0                                       | 0   |
| March 2011             | 0                                       | 0   |
| April 2011             | 0                                       | 0   |
| May 2011               | 0                                       | 0   |
| June 2011              | 0                                       | 0   |
| July 2011              | 0                                       | 0   |
| August 2011            | 0                                       | 0   |
| September 2011         | 0                                       | 0   |
| October 2011           | 0                                       | 0   |
| November 2011          | 0                                       | 0   |
| December 2011          | 0                                       | 0   |
| Overall Total          | 0                                       | 0   |

Annex K Cumulative Complaint and Summons/Prosecutions Log

#### ENVIRONMENTAL RESOURCES MANAGEMENT

Annex L

Construction Programme of the Project

| Activity<br>ID                               | Description   | Original<br>Duration | Early<br>Start             | Early<br>Finish        | DEC<br>28 05 12 19 26 | JAN<br>02 09 16 23 30    | FEB<br>06 13 20 27                               | MAR<br>05 12 19 26     | 02 09        |
|--|---|----------------------|----------------------------|------------------------|-----------------------|--------------------------|--|------------------------|--------------|
| <mark>minaries</mark><br>neral Requirem      | nents   |                      |                            |                        |                       |                          |  |                        |              |
| ontract Prelimi                              |   | 66                   | 14JUL2011 A                | 11JAN2012              |                       | PLW005310                |  |                        |              |
| PLW 005320                                   | Operation Plan - Approval   | 90                   | 12JAN2012                  | 10APR2012              |                       |                          |  |                        |              |
| <mark>gn and Design</mark><br>omission and C | Checking of Permanent Works   |                      |                            |                        |                       |                          |  |                        |              |
| ubmission and                                | l Approval  |                      |                            |                        |                       |                          |  |                        |              |
| DPD010361<br>DPD020361                       | DDA1: Design Memorandum - RtoC x 2<br>DDA2: Process Design- RtoC x 2                            |                      | 23SEP2011 A<br>30JUL2011 A | 29DEC2011<br>29DEC2011 |                       | DPD010361<br>DPD020361   | 1  |                        |              |
| DPD030330                                    | DDA3: Hydraulic Design- DC Checking   |                      | 09JUN2011 A                | 29DEC2011              |                       | DPD030330                |  |                        |              |
| DPD030360<br>DPD030361                       | DDA3: Hydraulic Design SO review<br>DDA3: Hydraulic Design RtoC x 2                             |                      | 02JAN2012<br>30JAN2012     | 29JAN2012<br>26FEB2012 |                       |                          | PD030360   | PD030361               |              |
| DPD040360                                    | DDA4: Plant Layout Drawing- SO review   |                      | 01JAN2012                  | 28JAN2012              |                       | DF                       | PD040360   |                        |              |
| DPD040361                                    | DDA4: Plant Layout Drawing- RtoC x2   |                      | 29JAN2012                  | 25FEB2012              |                       | DPD063140                | DP   | D040361                |              |
| DPD063140<br>DPD063175                       | DDA6: HAZOP Report- DC check final package<br>DDA6: HAZOP Report- SO rew. Final Package         | 30<br>28             | 29NOV2010 A<br>05JAN2012   | 04JAN2012<br>01FEB2012 |                       |                          | DPD063175  |                        |              |
| DPD071361                                    | DDA7A: P&ID RtoC x2   | 28                   | 19JUL2011 A                | 04JAN2012              |                       | DPD071361                | <br> <br> <br>                                   | <br> <br>              |              |
| DPD072360<br>DPD072361                       | DDA7B: Control Philosophy SO review<br>DDA7B: Control Philosophy RtoC x2                        |                      | 03NOV2011 A<br>31DEC2011   | 30DEC2011<br>27JAN2012 |                       | DPD072360                | D072361  |                        |              |
| PD073360                                     | DDA7C-G: SCADA system design- SO review   |                      | 03NOV2011 A                | 30DEC2011              |                       | DPD073360                |  |                        |              |
| 0PD073361<br>0PD074310                       | DDA7C-G: SCADA system design- RtoC x2<br>DDA7H-N-: SCADA Detail design- prep. Submission        |                      | 31DEC2011<br>25FEB2011 A   | 27JAN2012<br>03JAN2012 |                       | DPD074310                | D073361  |                        |              |
| DPD074330                                    | DDA7H-N-: SCADA Detail design- DC Checking  | 30                   | 04JAN2012                  | 14FEB2012              |                       |                          | DPD074330  | L<br>!<br>!            |              |
| DPD074360                                    | DDA7H-N-: SCADA Detail design- SO review  | 28                   | 18FEB2012                  | 16MAR2012              |                       |                          |  | DPD074360              | )            |
| DPD074361<br>DPD077161                       | DDA7H-N-: SCADA Detail design- RtoC x2<br>DDA8A: Pump sys design- RtoC x2                       | 28<br>28             | 17MAR2012<br>20AUG2011 A   | 13APR2012<br>01JAN2012 |                       | DPD077161                |  |                        |              |
| DPD077330                                    | DDA8B: Odour Duct design- DC Checking   |                      | 27MAY2011 A                | 30DEC2011              |                       | DPD077330                |  | ,<br>,<br>,<br>,       |              |
| 0PD077360<br>0PD077361                       | DDA8B: Odour Duct design- SO review DDA8B: Odour Duct design- RtoC x2                           |                      | 03JAN2012<br>31JAN2012     | 30JAN2012<br>27FEB2012 |                       |                          | DPD077360  | PD077361               |              |
| PD077710                                     | DDA8C: Pipe/Duct Supp. design- prep. Submission   | 60                   | 12MAY2011 A                | 11JAN2012              |                       | DPD077710                |  | 77700                  |              |
| OPD077730<br>OPD077760                       | DDA8C: Pipe/Duct Supp. design- DC Checking<br>DDA8C: Pipe/Duct Supp. design- SO review          | 30<br>28             | 12JAN2012<br>23FEB2012     | 22FEB2012<br>21MAR2012 |                       |                          | DPD0   | 77730<br>DPD07         | 77760        |
| DPD077761                                    | DDA8C: Pipe/Duct Supp. design- RtoC x2  |                      | 22MAR2012                  | 18APR2012              |                       | - <u> </u><br> <br> <br> | L<br>I<br>I                                      |                        |              |
| DPD081161<br>DPD084310                       | DDA9A-F: Elect. sys design- RtoC x2<br>DDA9K: Renewable Energy Design- prep. Submission         | -                    | 24AUG2011 A<br>18MAY2011 A |                        |                       | DPD081161                |  |                        |              |
| DPD084310<br>DPD084330                       | DDA9K: Renewable Energy Design- prep. Submission<br>DDA9K: Renewable Energy Design- DC Checking |                      | 03JAN2012                  | 13FEB2012              |                       |                          | DPD084330  |                        |              |
| DPD084360                                    | DDA9K: Renewable Energy Design- SO review   | 28                   | 17FEB2012                  | 15MAR2012              |                       |                          |  | DPD084360              |              |
| DPD084361<br>DPD084500                       | DDA9K: Renewable Energy Design- RtoC x2<br>DDA9L Elect Typ. Inst. Drg - prep Submission         | 28                   | 16MAR2012<br>04JUL2011 A   | 12APR2012<br>04JAN2012 |                       | DPD084500                |  |                        |              |
| DPD084510                                    | DDA9L Elect Typ. Inst. Drg - DC Checking  | 28                   | 05JAN2012                  | 01FEB2012              |                       |                          | DPD084510  |                        |              |
| DPD084520<br>DPD084530                       | DDA9L Elect Typ. Inst. Drg - DC Cert<br>DDA9L Elect Typ. Inst. Drg - Submit to SO               | 0                    | 02FEB2012                  | 01FEB2012              |                       |                          | <ul> <li>DPD084520</li> <li>DPD084530</li> </ul> |                        |              |
| DPD084540                                    | DDA9L Elect Typ. Inst. Drg - SO Review  |                      | 02FEB2012                  | 29FEB2012              |                       | - <del>1</del>           |  | DPD084540              |              |
| DPD084550<br>DPD084560                       | DDA9L Elect Typ. Inst. Drg - RtoC x2  | 28                   | 01MAR2012                  | 28MAR2012<br>28MAR2012 |                       |                          |  |                        | DPD084550    |
| DPD084560<br>DPD085200                       | DDA9L Elect Typ. Inst. Drg - SO Consent Granted<br>DDA10F BS Installation Drg - prep Submission | 30                   | 15JUN2011 A                | 28MAR2012<br>04JAN2012 |                       | DPD085200                |  |                        | P DI D004300 |
| DPD085210                                    | DDA10F BS Installation Drg - DC Checking  | 28                   | 05JAN2012                  | 01FEB2012              |                       |                          | DPD085210  | ,<br>,<br>,<br>,       |              |
| DPD085220<br>DPD085230                       | DDA10F BS Installation Drg - DC Cert<br>DDA10F BS Installation Drg - Submit to SO               | 0                    | 02FEB2012                  | 01FEB2012              |                       |                          | <ul> <li>DPD085220</li> <li>DPD085230</li> </ul> |                        |              |
| DPD085240                                    | DDA10F BS Installation Drg - SO Review  |                      | 02FEB2012                  | 29FEB2012              |                       |                          |  | DPD085240              |              |
| DPD085250<br>DPD085260                       | DDA10F BS Installation Drg - RtoC x2<br>DDA10F BS Installation Drg - SO Consent Granted         | 28                   | 01MAR2012                  | 28MAR2012<br>28MAR2012 |                       |                          |  |                        | DPD085250    |
| DPD090310                                    | DDA11: T&C Plan- prep. Submission   |                      | 01APR2011 A                | 22JAN2012              |                       | DPD090                   | <u>-</u><br>310                                  | <br>                   |              |
| DPD090330                                    | DDA11: T&C Plan- DC Checking  |                      | 23JAN2012                  | 02MAR2012              |                       |                          | -<br>  | DPD090330              | DPD090       |
| DPD090360<br>DPD090361                       | DDA11: T&C Plan- SO review<br>DDA11: T&C Plan- RtoC x2  |                      | 06MAR2012<br>03APR2012     | 02APR2012<br>30APR2012 |                       |                          |  |                        | DF D090      |
| DPD103151                                    | PTW: DDA 13A Elect Dwg - RtoC x2  |                      | 27JUL2011 A                | 12JAN2012              |                       | DPD103151                |  |                        |              |
| DPD103351<br>DPD150781                       | PTW: DDA 13C BS Dwg - RtoC x2<br>Septic: DDA14E Foundation - RtoC x2                            |                      | 27JUL2011 A<br>28NOV2011 A | 12JAN2012<br>17JAN2012 |                       | DPD103351                |  |                        |              |
| PD150796                                     | Septic: DDA14F Structure - RtoC x2  |                      | 210CT2011 A                |                        |                       | DPD150796                |  |                        |              |
| DPD151821                                    | Septic: DDA 14G Architecture - RtoC x2  | 28<br>28             | 17AUG2011 A                |                        |                       | DPD151821                |  |                        |              |
| 0PD153151<br>0PD153251                       | Septic: DDA14A Elect Dwg - RtoC x2<br>Septic: DDA14B Mech Dwg - RtoC x2                         |                      | 23AUG2011 A<br>09AUG2011 A |                        |                       | DPD153251                | <br>   | <br>                   |              |
| PD153351                                     | Septic: DDA14C BS Dwg - SO RtoC x 2   |                      | 28SEP2011 A                |                        |                       | DPD153351                |  |                        |              |
| PD153551<br>PD173610                         | Septic: DDA14D EMCR Dwg - RtoC x2<br>WB & Access: DDA 27A E&M Submission                        |                      | 24AUG2011 A<br>21MAR2011 A |                        |                       | DPD153551                |  |                        |              |
| PD173620                                     | WB & Access: DDA 27A E&M DC Checking  | 30                   | 03JAN2012                  | 13FEB2012              |                       |                          | DPD173620  |                        |              |
| PD173640                                     | WB & Access: DDA 27A E&M SO Rew & Appr.<br>WB & Access: DDA 27A E&M SO RtoC x 2.                | 28<br>28             | 14FEB2012<br>13MAR2012     | 12MAR2012<br>09APR2012 |                       |                          |  | DPD173640              |              |
| PD201711                                     | CEPT Tank: DDA 15G Architecture - RtoC x2   |                      | 28NOV2011 A                | 12JAN2012              |                       | DPD201711                |  |                        |              |
| PD203151<br>PD203351                         | CEPT: DDA 15A Elect Dwg - RtoC x2   | 28                   | 12SEP2011 A                |                        |                       | DPD203151                |  |                        |              |
| PD203351<br>PD300781                         | CEPT: DDA 15C BS Dwg - RtoC x2<br>UV: DDA 17E Foundation - RtoC x2                              | 28<br>28             | 18OCT2011 A<br>01SEP2011 A |                        |                       | DPD300781                | <br>   | <br>                   |              |
| PD300796                                     | UV: DDA 17F Structure - RtoC x2   |                      | 26NOV2011 A                |                        |                       | DPD300796                |  |                        |              |
| PD301821<br>PD303151                         | UV: DDA 17G Architectual - RtoC x2<br>UV: DDA 17A Elect Dwg - RtoC x2                           | 28<br>28             | 18AUG2011 A<br>10OCT2011 A |                        |                       | DPD301821<br>DPD303151   |  |                        |              |
| PD303251                                     | UV: DDA 17B Mech Dwg - RtoC x2  | 28                   | 100CT2011 A                | 07JAN2012              |                       | DPD303251                |  | r<br>1<br><del>-</del> |              |
| PD303350<br>PD303351                         | UV: DDA 17C BS Dwg - SO Review<br>UV: DDA 17C BS Dwg - RtoC x2                                  |                      | 23AUG2011 A<br>08JAN2012   | 07JAN2012<br>04FEB2012 |                       | DPD303350                | DPD303351  |                        |              |
| PD303551                                     | UV: DDA 17D E&MCR Dwg - RtoC x2   |                      | 25AUG2012                  | 12JAN2012              |                       | DPD303551                |  |                        |              |
| PD320781<br>PD320788                         | RWPS: DDA 21E Foundation - RtoC x2<br>RWPS: DDA 21F Structure - RtoC x2                         |                      | 05NOV2011 A<br>05NOV2011 A |                        |                       | DPD320781                |  |                        |              |
| PD320788                                     | RWPS: DDA 21F Structure - RtoC x2         RWPS: DDA 21G Mis Civil - RtoC x2                     | 28<br>28             | 17AUG2011 A                |                        |                       | DPD321011                |  |                        |              |
| PD323150                                     | RWPS: DDA 21A Elect Dwg - SO Review   |                      | 28SEP2011 A                | 12JAN2012              |                       | DPD323150                |  |                        |              |
| PD323151<br>PD323251                         | RWPS: DDA 21A Elect Dwg - RtoC x2         RWPS: DDA 21B Mech Dwg - RtoC x2                      | 28<br>28             | 13JAN2012<br>25AUG2011 A   | 09FEB2012<br>15JAN2012 |                       | DPD323251                | DPD323151  |                        |              |
| PD323251                                     | RWPS: DDA 21C BS Dwg - SO review  |                      | 070CT2011 A                | 17JAN2012              |                       | DPD323350                | <br> <br> <br>                                   | <br> <br> <br>         |              |
| PD323351                                     | RWPS: DDA 21C BS Dwg - SO RtoC x 2  | 28                   | 18JAN2012                  | 14FEB2012<br>07JAN2012 |                       | DPD323551                | DPD323351  |                        |              |
| PD323551<br>PD333200                         | RWPS: DDA 21D E&MCR Dwg - RtoC x2           RWPS: DAF Equipment SO rew & Appr                   | 28<br>120            | 30SEP2011 A<br>08NOV2011 A | 07JAN2012<br>17MAR2012 |                       |                          |  | DPD33320               | ю            |
| PD500781                                     | Chemical: DDA 22E Foundation - RtoC x2  | 28                   | 09NOV2011 A                | 11JAN2012              |                       | DPD500781                |  |                        |              |
| PD500788<br>PD501511                         | Chemical: DDA 22F Structure - RtoC x2<br>Chemical: DDA 22H Architectural - RtoC x2              | 28<br>28             | 09NOV2011 A<br>12NOV2011 A |                        |                       | DPD500788                | DPD  | 0501511                | <sup>1</sup> |
|  |   |                      |                            |                        |                       | 1                        |  | 1                      |              |


| Design, Build a        | and Operate Pillar Point Sewage Treatment Works                                 |                      |                        |                 | ATAL - Degremont - China State Joint Venture   |
|------------------------|---|----------------------|------------------------|-----------------|--|
| Activity<br>ID         | Description   | Original<br>Duration |                        | Early<br>Finish | 2011         2012           DEC         JAN         FEB         MAR         APR           28         05         12         19         26         02         09         16         23         30         06         13         20         27         05         12         19         26         02         09         16 |
| DPD503151              | Chemical: DDA 22A Elect Dwg - RtoC x2   | 28                   | 290CT2011 A            | 07JAN2012       | DPD503151  |
| DPD503251              | Chemical: DDA 22B Mech Dwg - RtoC x2  | 28                   | 30JUL2011 A            | 02JAN2012       | DPD503251  |
| DPD503330              | Chemical: DDA 22C BS Dwg - DC Checking  | 30                   | 30AUG2011 A            | 11JAN2012       | DPD503330  |
| DPD503350              | Chemical: DDA 22C BS Dwg - SO Review  | 28                   | 12JAN2012              | 08FEB2012       | DPD503350  |
| DPD503351              | Chemical: DDA 22C BS Dwg - RtoC x2  | 28                   | 09FEB2012              | 07MAR2012       | DPD503351  |
| DPD503551              | Chemical: DDA 22D E&MCR Dwg - SO rtoC x 2                                       | 28                   | 04NOV2011 A            | 21JAN2012       | DPD503551  |
| DPD513200              | Chemical: Chemical Dosing Equipment Approval                                    | 150                  | 01JUN2011 A            | 26FEB2012       | DPD513200  |
| DPD600741              | Sludge: DDA 16E Foundation - Rtoc x2  | 28                   | 16NOV2011 A            | 17JAN2012       | DPD600741  |
| DPD600981              | Sludge: DDA 16F Structural - RtoC x2  | 28                   | 18NOV2011 A            | 17JAN2012       | DPD600981  |
| DPD601330              | Sludge: DDA 16H Architectural - RtoC x2   | 28                   | 210CT2011 A            | 11FEB2012       | DPD601330  |
| DPD603151              | Sludge: DDA 16A Elect Dwg - RtoC x2   | 28                   | 10SEP2011 A            | 07JAN2012       | DPD603151  |
| DPD603251              | Sludge: DDA 16B Mech Dwg - RtoC x2  | 28                   | 30JUL2011 A            | 07JAN2012       | DPD603251  |
| DPD603351              | Sludge: DDA 16C BS Dwg - RtoC x2  | 28                   | 07SEP2011 A            |                 | DPD603351  |
| DPD603551              | Sludge: DDA 16D E&MCR Dwg - RtoC x2   | 28                   | 25AUG2011 A            | -               | DPD603551  |
| DPD700781              | DOU: DDA 18E Foundation - Rtoc x2   | 28                   | 03NOV2011 A            |                 | DPD700781  |
| DPD701005              | DOU: DDA 18G Checker Cert on Architecture                                       | 28                   | 09NOV2011 A            | -               | DPD701005  |
| DPD701010              | DOU: DDA 18G SO Review on Architecture  | 28                   | 11JAN2012              | 07FEB2012       | DPD701010  |
| DPD701011              | DOU: DDA 18G Architecture - RtoC x2   | 28                   | 08FEB2012              | 06MAR2012       | DPD701011  |
| DPD703150              | DOU: DDA 18A Elect Dwg - SO Review  | 28                   | 05SEP2011 A            | 17JAN2012       | DPD703150  |
|                        | •   | -                    |                        | -               | DPD703151  |
| DPD703151              | DOU: DDA 18A Elect Dwg - RtoC x2  | 28                   | 18JAN2012              | 14FEB2012       | DPD703251  |
| DPD703251              | DOU: DDA 18B Mech Dwg - RtoC x2   | 28                   | 02SEP2011 A            | 17JAN2012       |  |
| DPD703351              | DOU: DDA 18C BS Dwg - RtoC x2   | 28                   | 12OCT2011 A            |                 | DPD703351  |
| DPD703551              | DOU: DDA 18D E&MCR Dwg - RtoC x2  | 28                   | 24AUG2011 A            |                 | DPD703551  |
| DPD713201              | DOU: Equipment Submission SO Review   | 50                   | 05MAY2011 A            | 12JAN2012       | DPD713201  |
| DPD713202              | DOU: Equipment Submission - Approval  | 0                    |                        | 12JAN2012       | ◆ DPD713202  |
| DPD803351              | Admin Bldg: DDA 23C BS Dwg - RtoC x2  | 28                   | 23SEP2011 A            | 15JAN2012       | DPD803351  |
| DPD803551              | Admin Bldg: DDA 23B E&MCR Dwg - RtoC x2   | 28                   | 23SEP2011 A            | 11JAN2012       | DPD803551  |
| DPD902261              | Elect Bldg 1: DDA19E Foundation - RtoC x2                                       | 28                   | 05NOV2011 A            | 03JAN2012       | DPD902261  |
| DPD902511              | Elect Bldg 1: DDA19H Architecture - RtoC x2                                     | 28                   | 15NOV2011 A            | 08JAN2012       | DPD902511  |
| DPD902851              | Elect Bldg 1: DDA 19A Elect Dwg - RtoC x2                                       | 28                   | 22SEP2011 A            | 07JAN2012       | DPD902851  |
| DPD902881              | Elect Bldg 1: DDA 19C BS Dwg - RtoC x2  | 28                   | 26SEP2011 A            | 05JAN2012       | DPD902881  |
| DPD902895              | Elect Bldg 1: DDA 19D E&M CR Dwg - SO rew & Appr                                | 28                   | 22NOV2011 A            | 29DEC2011       | DPD902895  |
| DPD902896              | Elect Bldg 1: DDA 19D E&M CR Dwg - RtoC x 2                                     | 26                   | 30DEC2011              | 24JAN2012       | DPD902896  |
| DPD902930              | Elect Bldg 1: Elec Equipment SO Rew. & Appr                                     | 80                   | 14MAR2011 A            | 08JAN2012       | DPD902930  |
| DPD903461              | EB3/MCC Rms: DDA 20E Foundation - RtoC x2                                       | 28                   | 09NOV2011 A            | 07JAN2012       | DPD903461  |
| DPD903468              | EB2/3 PTWMCC: DDA 20F Structure - RtoC x2                                       | 28                   | 09NOV2011 A            | 30JAN2012       | DPD903468  |
| DPD903681              | EB3/MCC Rms: DDA 20H Architecture - RtoC x2                                     | 28                   | 24NOV2011 A            |                 | DPD903681  |
| DPD903850              | EB3/MCC Rms: DDA 20A Elect Dwg - SO Review                                      | 28                   | 140CT2011 A            |                 | DPD903850  |
| DPD903851              | EB3/MCC Rms: DDA 20A Elect Dwg - RtoC x2  | 28                   | 03JAN2012              | 30JAN2012       | DPD903851  |
| DPD903870              | EB3/MCC Rms: DDA 20C BS Dwg - DC Checking                                       | 30                   | 16AUG2011 A            |                 | DPD903870  |
| DPD903880              | EB3/MCC Rms: DDA 20C BS Dwg - SO Review   | 28                   | 12JAN2012              | 08FEB2012       | DPD903880  |
| DPD903881              | EB3/MCC Rms: DDA 20C BS Dwg - RtoC x2   | 28                   | 09FEB2012              | 07MAR2012       | DPD903881  |
| DPD903896              | EB3/MCC Rms: DDA 200 E&M CR Dg - RtoC x2  | 28                   | 12SEP2011 A            |                 | DPD903896  |
| DPD903940              | EB3/MCC Rms: ElecEquip't Checking & Appr  | 90                   | 14MAR2011 A            |                 | DPD903940  |
| DPD903940<br>DPD903954 | Refurbish: AIP 22A E&M GA Drg - SO Rew & Appr.                                  | 28                   | 07FEB2011 A            | 17JAN2012       | DPD903954  |
|                        |   | 35                   |                        | -               | DPD904001  |
| DPD904001              | Refurbish: DDA 25 E SHB Submission  |                      | 18APR2011 A            |                 | DPD904005  |
| DPD904005              | Refurbish: DDA 25 E Checker Cert on SHB   | 28                   | 12JAN2012              | 08FEB2012       | DPD904010  |
| DPD904010              | Refurbish: DDA 25 E SO Review SHB   | 28                   | 09FEB2012              | 07MAR2012       |  |
| DPD904011              | Refurbish: DDA 25 E SHB - RtoC x2   | 28                   | 08MAR2012              | 04APR2012       | DPD904011  |
| DPD904160              | Refurbish: DDA 25A~D E&M Dwg - Submission                                       | 60                   | 17JAN2011 A            | 07JAN2012       | DPD904160  |
| DPD904170              | Refurbish: DDA 25A~D E&M Dwg - DC Checking                                      | 30                   | 09JAN2012              | 17FEB2012       | DPD904170  |
| DPD904180              | Refurbish: DDA 25A~D E&M Dwg - SO Review  | 28                   | 20FEB2012              | 28MAR2012       | DPD904180  |
| DPD904181              | Refurbish: DDA 25A~D E&M Dwg - RtoC x2  | 28                   | 29MAR2012              | 07MAY2012       |  |
| DPD904710              | Flowmeter C: DDA 24E&F SO Review Fdn/Struct                                     | 28                   | 14OCT2011 A            |                 | DPD904710  |
| DPD904711              | Flowmeter C: DDA 24E&F Fdn/Struct - RtoC x2                                     | 28                   | 16JAN2012              | 12FEB2012       | DPD904711  |
| DPD904830              | Flowmeter C: DDA 24A~D E&M Dwg - SO rew &Appr                                   | 28                   | 01SEP2011 A            | 07JAN2012       | DPD904830  |
| DPD904831              | Flowmeter C: DDA 24A~D E&M Dwg - RtoC x2  | 28                   | 08JAN2012              | 04FEB2012       | DPD904831  |
| DPD916260              | Mis: DDA 28A Ext Civil Works Submission   | 100                  | 24JAN2011 A            | 18JAN2012       | DPD916260  |
| DPD916270              | Mis: DDA 28A Checker Cert Ext Civil Works                                       | 28                   | 19JAN2012              | 15FEB2012       | DPD916270  |
| DPD916280              | Mis: DDA 28A SO Review on Ext Civil Works                                       | 28                   | 16FEB2012              | 14MAR2012       | DPD916280  |
| DPD916281              | Mis: DDA 28A Ext Civil Works - RtoC x2  | 28                   | 15MAR2012              | 11APR2012       | DPD9   |
| DPD916302              | Mis: DDA 28B2 Checker Cert on Sitewide Drainage                                 | 28                   | 22SEP2011 A            | 05JAN2012       | DPD916302  |
| DPD916304              | Mis: DDA 28B2 SO Review on Sitewide Drainage                                    | 28                   | 06JAN2012              | 02FEB2012       | DPD916304  |
| DPD916306              | Mis: DDA 28B2 Sitewide Drainage RtoC x2   | 28                   | 03FEB2012              | 01MAR2012       | DPD916306  |
| DPD916310              | Mis: DDA 28B1 MH & Pipe Works Submission  | 100                  | 24JAN2011 A            | 10JAN2012       | DPD916310  |
| DPD916312              | Mis: DDA 28B1 Checker Cert on MH & Pipe Works                                   | 28                   | 11JAN2012              | 07FEB2012       | DPD916312  |
| DPD916314              | Mis: DDA 28B1 SO Review on MH & Pipe Works                                      | 28                   | 08FEB2012              | 06MAR2012       | DPD916314  |
| DPD916316              | Mis: DDA 28B1 MH & Pipe Works RtoC x2   | 28                   | 07MAR2012              | 03APR2012       | DPD916316  |
| DPD916410              | Mis: DDA 28B3 Watermain Submission  | 35                   | 12DEC2011 A            |                 | DPD916410  |
| DPD916412              | Mis: DDA 28B3 Watermain Submission<br>Mis: DDA 28B3 Checker Cert on Watermain   | 28                   | 26JAN2012              | 2255AN2012      | DPD916412  |
| DPD916412<br>DPD916414 | Mis: DDA 28B3 Checker Cert on Watermain<br>Mis: DDA 28B3 SO Review on Watermain | 28                   | 26JAN2012<br>23FEB2012 | 21MAR2012       | DPD916414  |
| DPD916414<br>DPD916416 | Mis: DDA 28B3 SO Review on Watermain<br>Mis: DDA 28B3 Watermain RtoC x2         | 28                   | 23FEB2012<br>22MAR2012 | 18APR2012       |  |
|                        |   |                      | 05DEC2011 A            |                 | DPD916420  |
| DPD916420              | Mis: DDA 28C1 Boundary Wall Submission  | 35                   |                        |                 | DPD916420  |
| DPD916421              | Mis: DDA 28C1 Checker Cert on Boundary Wall                                     | 28                   | 24JAN2012              | 20FEB2012       |  |

Contract No. DC/2008/03 Design, Build and Operate Pillar Point Sewage Treatment Works

ATAL - Degremont - China State Joint Venture



| ID           DPD923050           DPD923051           DPD923410           DPD923430           DPD923451           DPD923451           DPD923510           DPD923550           DPD923551           DPD923551           DPD923651           DPD923651           DPD926810           DPD926810           DPD926810           DPD927010           DPD927020 | Description         Mis: DDA 28C - SO Review         Mis: DDA 28C - RtoC x2         Mis: DDA 28F Mis BS - Submission         Mis: DDA 28F Mis BS - DC Checking         Mis: DDA 28F Mis BS - SO Review | Duration           28           28           60 | Start<br>29FEB2012<br>28MAR2012 | Finish<br>27MAR2012    | DEC JAN<br>18 05 12 19 26 02 09 16 23 | FEB<br>30 06 13 20 | MAR<br>27 05 12 19 26 | 02 09<br>023050 |
|--|--|---|---------------------------------|------------------------|---------------------------------------|--------------------|-----------------------|-----------------|
| PPD923051           PPD923450           PPD923450           PPD923451           PPD923510           PPD923550           PPD923551           PPD923551           PPD923551           PPD9236810           PPD926830           PPD926840           PPD926840           PPD927010   | Mis: DDA 28C - RtoC x2<br>Mis: DDA 28F Mis BS - Submission<br>Mis: DDA 28F Mis BS - DC Checking  | 28  |                                 | ZIWARZUIZ              | i i                                   |                    |                       | D323030         |
| PD923410<br>PD923430<br>PD923450<br>PD923451<br>PD923510<br>PD923550<br>PD923550<br>PD923551<br>PD926810<br>PD926830<br>PD926840<br>PD927010   | Mis: DDA 28F Mis BS - Submission<br>Mis: DDA 28F Mis BS - DC Checking  |   |                                 | 24APR2012              |                                       |                    |                       |                 |
| PD923430<br>PD923450<br>PD923451<br>PD923510<br>PD923530<br>PD923550<br>PD923551<br>PD926810<br>PD926830<br>PD926840<br>PD927010   | Mis: DDA 28F Mis BS - DC Checking  |   | 08APR2011 A                     |                        | DPD92                                 | 3410               |                       |                 |
| PD923450<br>PD923451<br>PD923510<br>PD923530<br>PD923550<br>PD923551<br>PD926810<br>PD926830<br>PD926840<br>PD926840   |  | 30  | 18JAN2012                       | 28FEB2012              |                                       |                    | DPD923430             |                 |
| PD923510<br>PD923530<br>PD923550<br>PD923551<br>PD926810<br>PD926830<br>PD926840<br>PD927010   |  | 28  | 29FEB2012                       | 27MAR2012              |                                       |                    | DF                    | PD923450        |
| PD923530<br>PD923550<br>PD923551<br>PD926810<br>PD926830<br>PD926840<br>PD927010   | Mis: DDA 28F Mis BS - RtoC x2  | 28  | 28MAR2012                       | 24APR2012              |                                       |                    |                       |                 |
| PD923550<br>PD923551<br>PD926810<br>PD926830<br>PD926840<br>PD927010   | Mis: DDA 28E E&M Dwg - Submission  | 60  | 08APR2011 A                     | 17JAN2012              | DPD92                                 | 3510               |                       |                 |
| PD923551<br>PD926810<br>PD926830<br>PD926840<br>PD927010   | Mis: DDA 28E E&M Dwg - DC Checking   | 30  | 18JAN2012                       | 28FEB2012              |                                       |                    | DPD923530             |                 |
| PD926810<br>PD926830<br>PD926840<br>PD927010   | Mis: DDA 28E E&M Dwg - SO Review   | 28  | 29FEB2012                       | 27MAR2012              |                                       |                    | DF                    | PD923550        |
| PD926830<br>PD926840<br>PD927010   | Mis: DDA 28E E&M Dwg - Rtoc x2   | 28  | 28MAR2012                       | 24APR2012              |                                       |                    |                       | 1               |
| PD926840<br>PD927010   | Mis: Solid Handling Bldg Eq. Submission  | 60  | 18JAN2011 A                     | 10JAN2012              | DPD926810                             |                    |                       |                 |
| PD927010   | Mis: Guard House Equipment Submission  | 60  | 18JAN2011 A                     | 07JAN2012              | DPD926830                             |                    |                       |                 |
|  | Mis: E&M Equipment Checking and Approval   | 90  | 11JAN2012                       | 09APR2012              | DPD927010                             |                    |                       |                 |
| PD977070   | WB at Egress: DDA 27G&H - Structure Submission   | 30  | 01DEC2011 A                     | 10JAN2012              | DFD927010                             | DPD927             | 120                   |                 |
|  | WB at Egress: DDA 27G&H - DC Check on Structure  | 28  | 11JAN2012<br>18FEB2012          | 17FEB2012              |                                       | DFD927             | DPD927                | 030             |
| PD927030<br>PD927040   | WB at Egress: DDA 27G&H -SO Comment on Structure<br>WB at Egress: DDA 27G&H -Structure RtoC x2   | 28<br>28  | 18FEB2012<br>22MAR2012          | 21MAR2012<br>27APR2012 |                                       |                    | DF D927               | _!              |
| PD928130   | CLP Sub: AIP26B - Structure Design Submission  | 35  | 22101AR2012<br>28NOV2011 A      | -                      | DPD928130                             |                    |                       |                 |
| PD928130   | CLP Sub: AIP26B - Checker Cert on Structure  | 28  | 13JAN2012                       | 09FEB2012              |                                       | DPD928140          |                       |                 |
| PD928140<br>PD928150   | CLP Sub: AIP26B - SO Approval on Structure   | 28  | 10FEB2012                       | 09FEB2012              |                                       |                    | DPD928150             |                 |
| PD928150<br>PD928160   | CLP Sub: DDA29A - E&M GA & CR Drg Subm   | 30  | 21NOV2011 A                     | 17JAN2012              | DPD92                                 | 8160               |                       |                 |
| PD928170   | CLP Sub: DDA29A - E&M GA & CR Drg DC Check   | 28  | 18JAN2012                       | 14FEB2012              |                                       | DPD928170          |                       |                 |
| PD928180   | CLP Sub: DDA29A - E&M GA & CR Drg SO Review  | 28  | 15FEB2012                       | 13MAR2012              |                                       |                    | DPD928180             |                 |
| PD928190   | CLP Sub: DDA29A - E&M GA & CR Drg RtoC x2  | 28  | 14MAR2012                       | 10APR2012              |                                       |                    |                       |                 |
| PD928200   | CLP Sub: DDA29E - Foundation Submission  | 28  | 13JAN2012                       | 09FEB2012              |                                       | DPD928200          |                       |                 |
| PD928210   | CLP Sub: DDA29E - DC Check on Foundation   | 28  | 10FEB2012                       | 08MAR2012              |                                       |                    | DPD928210             |                 |
| PD928220   | CLP Sub: DDA29E - SO Comment on Foundation   | 28  | 09MAR2012                       | 05APR2012              |                                       |                    |                       | DPD             |
| DPD928230  | CLP Sub: DDA29E - Foundation RtoC x2   | 28  | 06APR2012                       | 03MAY2012              |                                       |                    |                       |                 |
| PD928300   | CLP Sub: DDA29F - Structure Submission   | 28  | 13JAN2012                       | 09FEB2012              |                                       | DPD928300          |                       |                 |
| PD928310   | CLP Sub: DDA29F - DC Check on Structure  | 28  | 10FEB2012                       | 08MAR2012              |                                       |                    | DPD928310             |                 |
| PD928320   | CLP Sub: DDA29F - SO Comment on Structure  | 28  | 09MAR2012                       | 05APR2012              |                                       |                    |                       | DPD9            |
| PD928330   | CLP Sub: DDA29F - Structure RtoC x2  | 28  | 06APR2012                       | 03MAY2012              |                                       |                    |                       |                 |
| PD928400   | CLP Sub: DDA29G - Architecture Submission  | 28  | 13JAN2012                       | 09FEB2012              |                                       | DPD928400          |                       |                 |
| DPD928410  | CLP Sub: DDA29G - DC Check on Architecture   | 28  | 10FEB2012                       | 08MAR2012              |                                       |                    | DPD928410             |                 |
| DPD928420  | CLP Sub: DDA29G - SO Comment on Architecture   | 28  | 09MAR2012                       | 05APR2012              |                                       |                    |                       | DPD9            |
| DPD928430  | CLP Sub: DDA29G - Architecture RtoC x2   | 28  | 06APR2012                       | 03MAY2012              |                                       |                    |                       |                 |
| atutory Submiss  |  |   |                                 |                        |                                       |                    |                       |                 |
| Submission and SS0100050   | DSD &ASD - GBP Submission and Approval   | 60  | 29NOV2010 A                     | 17JAN2012              | SS0100                                | 0050               |                       |                 |
| SS0100400  | EPD - Sewage Discharge License Approval  | 90  | 06JUN2011 A                     | 02MAR2012              |                                       |                    | SS0100400             |                 |
| S0100410   | EPD - Approval for Sewage Discharge  | 0   |                                 | 02MAR2012              |                                       |                    | ♦ SS0100410           |                 |
| SS0110700  | WSD & ASD- Approve Water Supply /Plumbing issue  | 80  | 29NOV2010 A                     |                        |                                       | SS0110700          |                       |                 |
| S0110810   | EPD - Register of Changes under Environ. Permit  | 100   | 13SEP2010 A                     | 08FEB2012              |                                       | SS0110810          |                       |                 |
| SS0121000  | VCAB Submission and Approval   | 300   | 13SEP2010 A                     | 08MAR2012              |                                       |                    | SS0121000             |                 |
| S0122100   | ArchSD Submission and Approval (Stage 1)   | 150   | 13SEP2010 A                     | 04JAN2012              | SS0122100                             |                    |                       |                 |
| SS0122200  | ArchSD Submission and Approval (Stage 2)   | 120   | 05JAN2012                       | 06JUN2012              |                                       |                    |                       |                 |
| and Structural   |  |   |                                 |                        |                                       |                    |                       |                 |
|  | nced Primary Treatement System   |   |                                 |                        |                                       |                    |                       |                 |
| uilding and Structure CCC200145  | CEPT: Delivery of E&M Cast-in Item (3)   | 0   |                                 | 30DEC2011              | ◆ CCC200145                           |                    |                       |                 |
| CC200145   | CEPT: Delivery of E&M Cast-in Item (3)   | 0   |                                 | 03FEB2012              | • • • • • • • • •                     | ♦ CCC200146        |                       |                 |
| CC200140   | CEPT Tank: Superstructure-Grd Floor Slab   | 90  | 26MAR2012                       | 23JUN2012              |                                       |                    |                       |                 |
| CC200180   | CEPT Tank: Backfilling   | 135   | 30JAN2012                       | 12JUN2012              |                                       |                    |                       |                 |
| CC200240   | CEPT Tank: Water Test at Bay 2 Zone 1  | 30  | 29DEC2011                       | 01FEB2012              |                                       | CCC200240          |                       |                 |
| CC200250   | CEPT Tank: Bay 2 Zone 2 Wall   | 80  | 05NOV2011 A                     | 17JAN2012              | CCC20                                 | 0250               |                       | - <br> <br>     |
| CC200255   | CEPT Tank: Water Test Bay 2 Zone 2   | 25  | 02FEB2012                       | 26FEB2012              |                                       |                    | CCC200255             |                 |
| CC200270   | CEPT Tank: West Channel Bay 2 Zone 2   | 20  | 29DEC2011                       | 18JAN2012              | CCC2                                  | 00270              |                       |                 |
| CCC200280  | CEPT Tank: Bay 4 Zone 3 Wall   | 75  | 29DEC2011                       | 17MAR2012              |                                       |                    | CCC200280             |                 |
| CC200285   | CEPT Tank: Water Test at Bay 4 Zone 3  | 25  | 24MAR2012                       | 17APR2012              |                                       |                    |                       |                 |
| CC200290   | CEPT Tank: West Corridor Slab Bay 4 Zone 3   | 25  | 23DEC2011 A                     | 17JAN2012              | CCC20                                 | 0290               |                       |                 |
| CC200300   | CEPT Tank: West Channel Bay 4 Zone 3   | 20  | 01MAR2012                       | 20MAR2012              |                                       |                    | CCC2003               |                 |
| CC200310   | CEPT Tank: West Bay 4 Zone 4 Wall  | 75  | 08JAN2012                       | 27MAR2012              |                                       | I.                 | CO                    | CC200310        |
| CC200320   | CEPT Tank: West Corridor Slab Bay 4 Zone 4   | 25  | 27DEC2011 A                     | 19JAN2012              | CCC                                   | 200320             |                       |                 |
| CC200330   | CEPT Tank: West Channel Bay 4 Zone 4   | 20  | 21MAR2012                       | 09APR2012              |                                       |                    |                       |                 |
| CC200340   | CEPT Tank: Bay 5 Wall  | 75  | 02NOV2011 A                     |                        |                                       | CCC200340          |                       |                 |
| CCC200345  | CEPT Tank: Water Test to Bay 5 Wall  | 25  | 19FEB2012                       | 14MAR2012              |                                       | 000000050          | CCC200345             |                 |
| CC200350   | CEPT Tank: West Corridor Slab Bay 5  | 30  | 14DEC2011 A                     |                        |                                       | CCC200350          |                       | 0000            |
| CC200360   | CEPT Tank: West Channel Bay 5  | 20  | 03MAR2012                       | 22MAR2012              |                                       |                    | CCC20                 | 0360            |
| CC200370   | CEPT : Bay 1 Zone 1 East Walls   | 100   | 29DEC2011                       | 11APR2012              |                                       |                    |                       |                 |
| CC200380   | CEPT : Bay 1 Zone 2 East Walls   | 100   | 12JAN2012                       | 25APR2012              |                                       |                    |                       |                 |
| 000000   | CEPT : Bay 3 Zone 3 East Walls   | 100   | 31JAN2012                       | 09MAY2012              |                                       |                    |                       |                 |
|  | CEPT : Bay 3 Zone 4 East Walls   | 100   | 14FEB2012                       | 23MAY2012              |                                       |                    |                       |                 |
| CC200400   |  | 400   | 01550040                        |                        |                                       |                    |                       |                 |
| CC200390<br>CC200400<br>CC200410<br>CC200415   | CEPT : Bay 5 Eastern Walls<br>CEPT : Water Test to East Tanks  | 100<br>84                                       | 01FEB2012<br>18MAR2012          | 10MAY2012<br>09JUN2012 |                                       |                    |                       |                 |

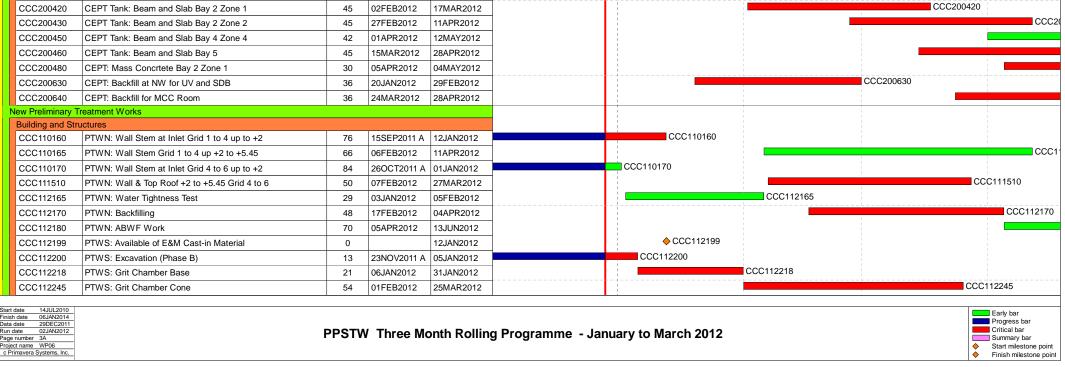

|                            |   |                      | -                      |                        | 2012                                  |         |
|----------------------------|---|----------------------|------------------------|------------------------|---------------------------------------|---------|
| Activity<br>ID             | Description   | Original<br>Duration | Early<br>Start         | Early<br>Finish        | JAN FEB MAR                           | AP      |
| C112320                    | PTWS: Raft Footing for Channel  | 7                    | 26MAR2012              | 01APR2012              |                                       | CCC112  |
| C113110                    | PTWS: Grit Chamber (Upper Chamber Wall) 1 & 2                                   | 20                   | 19MAR2012              | 07APR2012              |                                       | C       |
| 114100                     | PTWS: Formation of Fine Screen Chamber  | 10                   | 31MAR2012              | 09APR2012              |                                       |         |
| C150010                    | PTW: MCC Room PTW: Formation to MCC Room  | 75                   | 05APR2012<br>05APR2012 | 18JUN2012<br>07APR2012 |                                       | C       |
| ction Systen               |   | 3                    | 03AFK2012              | 074FK2012              |                                       |         |
| ing and Stru               |   |                      |                        |                        |                                       |         |
| 300130                     | UV: Excavation  | 24                   | 27JAN2012              | 23FEB2012              | CCC300130                             |         |
| 300131                     | UV: Outlet Pit  | 20                   | 24FEB2012              | 17MAR2012              | CCC300131                             |         |
| 300132                     | UV: Vertical Blinding   | 8                    | 18MAR2012              | 25MAR2012              | CCC30                                 | 00132   |
| 300136                     | UV: Backfill and Formation to Channel   | 10                   | 26MAR2012              | 06APR2012              |                                       | CC      |
| 300138                     | UV: Inlet & Outlet Channel  | 20                   | 07APR2012              | 04MAY2012              |                                       |         |
|                            | UV: Raft Foundation 900mm thk   | 20                   | 07APR2012              | 04MAY2012              |                                       |         |
| Treatment F                |   |                      |                        |                        |                                       |         |
| ing and Stru<br>600230     | ctures<br>SDB: Southern Raft Foundation - 1500mm thk                            | 14                   | 29DEC2011 A            | 14JAN2012              | CCC600230                             |         |
|                            |   |                      |                        |                        | CCC600250                             |         |
| C600250                    | SDB: Southern Holding Tanks (Bottom Pour)<br>SDB: Remove Formwork and Clearance | 18                   | 16JAN2012<br>11FEB2012 | 10FEB2012<br>16FEB2012 | CCC600250                             |         |
| C600260                    | SDB: Remove Formwork and Clearance<br>SDB: Install Temporary Strut at +4.0      | 6                    | 11FEB2012<br>17FEB2012 | 16FEB2012<br>23FEB2012 | CCC600270                             |         |
| 600270<br>600280           | SDB: Install Temporary Strut at +4.0<br>SDB: Excavation for North Part          | 10                   | 17FEB2012<br>24FEB2012 | 23FEB2012<br>06MAR2012 | CCC600280                             |         |
|                            | SDB: Excavation for North Part<br>SDB: Northern Raft Foundation - 1500mm thk    | 10                   | 07MAR2012              | 23MAR2012              | CCC6002200                            | 290     |
| C600290                    | SDB: Northern Holding Tanks (Bottom Pour)                                       | 15                   | 24MAR2012              | 10APR2012              |                                       |         |
| ry Building                |   | 14                   |                        |                        |                                       |         |
| ing and Stru               | ctures  |                      |                        |                        |                                       |         |
| -                          | Chemical Bldg: Excavation   | 12                   | 31MAR2012              | 18APR2012              |                                       |         |
| 800140                     | Admin Bldg: Underground Drainage Work   | 10                   | 02JAN2012              | 11JAN2012              | CCC800140                             |         |
| 800155                     | Admin Bldg: Ground Beam   | 12                   | 15DEC2011 A            | 01JAN2012              | CCC800155                             |         |
| 2800160                    | Admin Bldg: Beams & Slab at G/F   | 12                   | 14JAN2012              | 30JAN2012              | CCC800160                             |         |
| 800200                     | Admin Bldg: Water Tank - Roof Slab & Beams                                      | 10                   | 31JAN2012              | 09FEB2012              | CCC800200                             |         |
| 800220                     | Admin Bldg: Walls & Columns - G/F to 1/F  | 15                   | 31JAN2012              | 14FEB2012              | CCC800220                             |         |
| C800230                    | Admin Bldg: Beams & Slab at 1/F   | 11                   | 15FEB2012              | 25FEB2012              | CCC800230                             |         |
| C800240                    | Admin Bldg: Walls & Columns - 1/F to R/F  | 14                   | 26FEB2012              | 10MAR2012              | CCC800240                             |         |
| C800250                    | Admin Bldg: Beams & Slab at R/F   | 12                   | 11MAR2012              | 22MAR2012              | CCC80025                              | 50      |
| C800260                    | Admin Bldg: Walls & Columns - R/F to TRF  | 10                   | 23MAR2012              | 01APR2012              |                                       | CCC800  |
| C800270                    | Admin Bldg: Beams & Slab at TR/F  | 10                   | 02APR2012              | 11APR2012              |                                       |         |
| 0800280                    | Admin Bldg: ABWF Works  | 60                   | 21MAR2012              | 19MAY2012              |                                       |         |
| C910110                    | Elect Bldg 1: Excavation  | 12                   | 09JAN2012              | 27JAN2012              | CCC910110                             |         |
| C910115                    | Elect Bldg 1: Demolish Canopy of Extg Tx Room                                   | 6                    | 28JAN2012              | 03FEB2012              | CCC910115                             |         |
| C910120                    | Elect Bldg 1: Fdn-Cable Trench &On-Grade Slab                                   | 20                   | 04FEB2012              | 27FEB2012              | CCC910120                             |         |
| C910130                    | Elect Bldg 1: Walls - G/F to R/F  | 24                   | 28FEB2012              | 26MAR2012              | CCC9                                  | 910130  |
| C910140                    | Elect Bldg 1: Roof Slab   | 18                   | 27MAR2012              | 20APR2012              |                                       |         |
| C930110                    | Elect Bldg 3: Excavation  | 6                    | 16FEB2012              | 22FEB2012              | CCC930110                             |         |
| C930120                    | Elect Bldg 3: Fdn-Cable Trench &On-Grade Slab                                   | 18                   | 23FEB2012              | 14MAR2012              | CCC930120                             |         |
| 0930130                    | Elect Bldg 3: Walls - G/F to R/F  | 12                   | 15MAR2012              | 28MAR2012              |                                       | C930130 |
|                            | Elect Bldg 3: Roof Slab   | 24                   | 29MAR2012              | 30APR2012              |                                       |         |
| laneous Wor<br>ellaneous W |   |                      |                        |                        |                                       |         |
| M102000                    | Installation of Sitewide Sewerage   | 380                  | 28MAR2012              | 13JUL2013              |                                       |         |
| M102020                    | Pipe Line bet N2 to PTW and Manholes N2 & N3                                    | 150                  | 05APR2012              | 060CT2012              |                                       |         |
| y Works                    |   |                      |                        |                        |                                       |         |
| ssion and Co               |   |                      |                        |                        |                                       |         |
| nission and A<br>0050310   | Approval<br>DDA5: Utilities- prep. Submission                                   | 60                   | 25JUL2011 A            | 13JAN2012              | DPD050310                             |         |
|                            | DDA5: Utilities- Submit to DC   | 0                    | LOUGLEONA              | 13JAN2012              | ♦ DPD050320                           |         |
| 050330                     | DDA5: Utilities- DC Checking  | 30                   | 14JAN2012              | 12FEB2012              | DPD050330                             |         |
| 050340                     | DDA5: Utilities- DC Cert  | 0                    |                        | 12FEB2012              | ♦ DPD050340                           |         |
|                            | DDA5: Utilities-submit to SO  | 0                    | 13FEB2012              |                        | ◆ DPD050350                           |         |
|                            | DDA5: Utilities- SO review  | 56                   | 16FEB2012              | 11APR2012              |                                       |         |
| orks                       |   |                      |                        |                        |                                       |         |
| ement and Ir               |   |                      |                        |                        |                                       |         |
| ing and Stru               |   |                      |                        |                        |                                       |         |
|                            | Grit: E&M Equipment Procurement   | 180                  | 21NOV2011 A            | -                      |                                       | EM      |
|                            | Grit: Delivery of E&M Equipment On Site   | 42                   | 07APR2012              | 18MAY2012              |                                       |         |
| V301100                    | UV: E&M Equipment Procurement   | 180                  | 08FEB2012              | 05AUG2012              |                                       |         |
| V322200                    | RWPS: E&M Equipment Procurement   | 210                  | 26MAR2012              | 210CT2012              |                                       |         |
| V501000                    | Chemical: E&M Equipment Procurement   | 150                  | 14MAR2012              | 10AUG2012              | · · · · · · · · · · · · · · · · · · · |         |
|                            | Sludge: E&M Equipment Procurement   | 240                  | 08JAN2012              | 03SEP2012              |                                       |         |
|                            | DOU A: E&M Equipment Procurement  | 180                  | 28FEB2012              | 25AUG2012              |                                       |         |
|                            | DOU B: E&M Equipment Procurement  | 180                  | 13JAN2012              | 10JUL2012              |                                       |         |
| V802100                    | Admin Bldg : SCADA Eq. Procurement  | 80                   | 22FEB2012              | 11MAY2012              |                                       |         |
|                            | Admin Bldg : ELV Eq. Procurement  | 60                   | 30MAR2012              | 28MAY2012              |                                       |         |
| V941600                    | Elect Bldg 1: BS Modification on existing room                                  | 7                    | 06JAN2012              | 13JAN2012              | EMW941600                             |         |
| V942100                    | CB Main SW Rm: Mat'l & Equipment Procurement                                    | 180                  | 10JAN2012              | 07JUL2012              |                                       |         |

| Start date 14JUL2010  |   | Early bar              | 1 |
|---|---|------------------------|---|
| Finish date 06JAN2014   |   |                        |   |
| Data date 29DEC2011   |   | Progress bar           |   |
| Run date 02JAN2012  | PDSTW/ Three Month Polling Programme January to March 2012  | Critical bar           |   |
| Data date 29DEC2011<br>Run date 02JAN2012<br>Page number 4A<br>Project name WP06<br>c Primavera Systems, Inc. | PPSTW Three Month Rolling Programme - January to March 2012 | Summary bar            |   |
| Project name WP06   |   | Start milestone point  |   |
| c Primavera Systems, Inc.   |   | Finish milestone point |   |
