

## TABLE OF CONTENTS

|                                                                                                                 | Page |
|-----------------------------------------------------------------------------------------------------------------|------|
| EXECUTIVE SUMMARY                                                                                               | 1    |
| 行政摘要                                                                                                            | 1    |
| 1 INTRODUCTION                                                                                                  | 3    |
| 1.1 Background                                                                                                  | 3    |
| 1.2 Scope of Report                                                                                             | 4    |
| 1.3 Project Organization                                                                                        | 4    |
| 1.4 Summary of Construction Works                                                                               | 5    |
| 2 SUMMARY OF EM&A PROGRAMME REQUIREMENTS                                                                        | 6    |
| 2.1 Monitoring Parameters and Locations                                                                         | 6    |
| 2.2 Environmental Quality Performance Limits (Action/Limit Levels)                                              | 6    |
| 2.3 Environmental Mitigation Measures                                                                           | 6    |
| 3 NOISE MONITORING                                                                                              | 7    |
| 4 WATER QUALITY MONITORING                                                                                      | 8    |
| 5 LAND CONTAMINATION MONITORING                                                                                 | 8    |
| 5.1 Monitoring Status                                                                                           | 8    |
| 5.2 Excavation Progress                                                                                         | 8    |
| 5.3 Biopiling and Cement Solidification / Stabilization Progress                                                | 8    |
| 5.4 Landfill Disposal Progress                                                                                  | 8    |
| 5.5 IEA Spot Check Samples                                                                                      | 9    |
| 6 ENVIRONMENTAL SITE INSPECTION AND AUDIT                                                                       | 10   |
| 7 ADVICE ON SOLID AND LIQUID WASTE MANAGEMENT STATUS                                                            | 11   |
| 8 SUMMARY OF NON-COMPLIANCE (EXCEEDANCES) OF ENVIRONMENTAL QUALITY PERFORMANCE LIMITS (ACTION AND LIMIT LEVELS) | 11   |
| 9 COMPLAINT, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTION                                                 | 11   |
| 10 COMMENTS, RECOMMENDATIONS AND CONCLUSIONS                                                                    | 12   |
| 10.1 Comments on Mitigation Measures                                                                            | 12   |
| 10.2 Recommendations on EM&A Programme                                                                          | 12   |
| 10.3 Conclusions                                                                                                | 13   |

## List of Tables

Table 1.1 Contact Information of Key Personnel

Table 2.1 Locations of Impact Noise Monitoring Stations

Table 2.2 Noise Monitoring Parameters, Frequency and Duration

Table 3.1 Summary of Number of Exceedances for Construction Impact Noise Monitoring

Table 9.1 Summary of Environmental Complaints, Summons and Successful Prosecutions

## List of Figures

- Figure 1 Site Location Plan
- Figure 2 Noise Monitoring Locations
- Figure 3 Environmental Complaint Handling Procedure
- Figure 4 Locations of Contamination Zones
- Figure 5 Locations of Confirmatory Sampling (Zones R5 & R6)
- Figure 6 Locations of Confirmatory Sampling (Zones R1 & R7)
- Figure 7 Locations of Confirmatory Sampling (Zones R2 & R3)
- Figure 8 Locations of Confirmatory Sampling (Zones R4 & R8)
- Figure 9 Locations of Confirmatory Sampling (Zone A1)
- Figure 10 Locations of Confirmatory Sampling (Zones A2, A3, A4 & A5)
- Figure 11 Locations of Confirmatory Sampling (Zones T32C, T32D, T32E, T35C & T36A)
- Figure 12 Locations of Confirmatory Sampling (Zones T19A, T22BA, T22BB)
- Figure 13 Locations of Confirmatory Sampling (Zone T32E)
- Figure 14 Locations of Confirmatory Sampling (Zone T35C)

## List of Appendices

- Appendix A Project Organization Structure
- Appendix B Construction Programme
- Appendix C Implementation Schedule of Environmental Mitigation Measures (EMIS)
- Appendix D Summary of Action and Limit Levels
- Appendix E Graphical Presentation of Impact Daytime Construction Noise Monitoring Results over past four months
- Appendix F Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

## EXECUTIVE SUMMARY

The proposed “Yau Tong Bay – Decommissioning of Shipyard Sites” (hereinafter referred to as “the Project”) is a Designated Project under the Environmental Impact Assessment Ordinance (Cap. 499) Schedule 2 and is governed by the Environmental Permit No. EP-409/2010. The Project aims to demolish the past and existing shipyards and their building structures and marine structures and decontaminate identified contaminated spots.

The demolition works of the building structures on land commenced on 21 November 2011 and was completed in September 2012. The demolition works of marine structures are yet to commence.

The impact Environmental Monitoring and Audit (hereinafter referred to as “EM&A”) programme for the Project commenced on 21 November 2011. The EM&A works was suspended from November 2012 for the captioned Project and the EM&A works has been resumed on 28 October 2013. The impact EM&A programme includes daytime construction noise and water quality monitoring, soil remediation works monitoring and auditing and site auditing. The remediation method statement was approved by the EPD on 20 December 2013. The soil remediation works commenced on 23 December 2013.

This report documents the findings of EM&A works conducted in the quarter between 1 July 2014 and 30 September 2014.

As informed by the Contractor, the major construction activities carried out in the reporting quarter were:

- Backfill to Zones R3, R5, R6, R7, R8, A3, A4, T22BA, T22BB, T32C, T32E (inner) and T35C;
- Cleanup progress monitoring of Biopiles; and
- Disposal of contaminated soil in Zone T32E to the South East New Territories (SENT) Landfill.
- Closure Assessment Sampling of Biopile.

A summary of monitoring and audit activities conducted in the reporting quarter is listed below:

|                               |             |
|-------------------------------|-------------|
| Daytime noise monitoring      | 7 sessions  |
| Water quality monitoring      | 0 session   |
| Environmental site inspection | 13 sessions |

### Breaches of Action and Limit Levels for Daytime Construction Noise

No Action Level exceedance was recorded since no construction noise related complaint was received in the reporting quarter.

No Limit Level exceedance of construction noise was recorded in the reporting quarter.

### Breaches of Action and Limit Levels for Water Quality

Water quality monitoring was not conducted in the reporting quarter as the demolition of marine structures was not commenced.

### Environmental Complaint, Notification of Summons and Successful Prosecution

No environmental complaint, notification of summons and successful prosecution was received in the reporting quarter.

### Reporting Change

There was no reporting change required in the reporting quarter.

### Future Key Issues

Key issues to be considered in the coming month include:

- Proper storage and labeling of oils and chemicals on site;
- Chemical, chemical waste and waste management;
- Proper maintenance of all drainage facilities and wheel washing facilities on site;
- Dust suppression from excavation activities and haul road traffic; and
- Tree protective measures for all retained trees.

## 行政摘要

「油塘灣—船廠拆卸工程」(以下簡稱「本工程項目」)是一項被臚列於環境影響評估條例(第 499 章)附表 2 中的

指定工程項目並受到環境許可證編號 EP-409/2010 所管制。本工程項目的主要目的是要拆除位於油塘灣的舊有和現有的船廠及其建築物和海事結構，以及處理指定的已受污染點。

船廠陸上建築物的拆卸工程於二零一一年十一月二十一日展開，並於二零一二年九月完工。船廠海上建築物的拆除工作尚未開始。本工程項目之施工期間環境監察與審核工作暫停，並於二零一三年十月二十八日恢復。施工期間環境監察與審核計劃包括：日間建築噪音監測，水質監測，已受污染泥復育工作的監察與審核及工地審核巡查。環保署在二零一三年十二月二十日批准了土地整治方法聲明。土壤修復工程於二零一三年十二月二十三日開始。

本報告記錄了於 2014 年 7 月 1 日至 2014 年 9 月 30 日期間所進行的環境監察與審核工作。根據承建商提供的資料，在上述的季度的主要建築活動為：

- 在區域 R3、R5、R6、R7、R8、A3、A4、T22BA、T22BB、T32C、T32E（內部）和 T35C 的回填、
- 生物堆封閉評估抽樣、
- 在新界東南堆填區處置區域 T32E 的污染土壤，以及
- 生物堆清理進度監控。

在上述的季度有下列次數的監察及審核活動進行：

|          |      |
|----------|------|
| 日間建築噪音監測 | 7 次  |
| 水質監測     | 0 次  |
| 環境巡查     | 13 次 |

### 違反監測標準

#### 日間建築噪音

在上述的期間沒有收到有關建築噪音的投訴，所以噪音監測結果皆符合行動水平。在上述的季度的所有日間建築噪音監測結果皆符合極限水平。

#### 水質

因為相關的海事結構拆除工程仍未開始，故沒有水質監測在上述的季度進行。因此，沒有違反水質行動水平和極限水平的記錄。

### 有關收到的環境的投訴，傳票及檢控

在上述的季度沒有收到有關環境的投訴、傳票或檢控。

### 報告修訂

本報告季度並沒有修訂報告。

### 預計要注意的事項

- 正確保存油類和化學品；
- 化學廢物和廢物管理；
- 正確保養所有排水設施和車輪清洗設施；
- 抑制從發掘活動和運輸道路交通的灰塵；和
- 對保留樹木的保護措施。

## 1 INTRODUCTION

### 1.1 Background

- 1.1.1. The Project Site of “Yau Tong Bay-Decommissioning of Shipyard Sites” (hereinafter referred to as “the Project”) is located along the shore of Yau Tong Bay (which is also known as Kwun Tong Tsai Wan) in East Kowloon within the Kwun Tong District and the Project Site together with its adjacent land is zoned Comprehensive Development area (“CDA”) on the Approved Cha Kwo Ling, Yau Tong, Lei Yue Mun Outline Zoning Plan (OZP) No. S/K15/19. It faces Victoria Harbour to the southwest and is bounded by the Eastern Harbour Crossing Ventilation Building to the west, Cha Kwo Ling Road to the north and east, and Ko Fai Road to the south. The site is also adjacent to the former Yau Tong Industrial Area, which is at present mainly occupied by obsolete industrial buildings.
- 1.1.2. The Project is a designated project and is governed by the Environmental Permit No. EP-409/2010 (hereinafter referred to as “the EP”).
- 1.1.3. Major works to be undertaken in the Project include:-
- Demolition of past and existing shipyard and building structures;
  - Demolition of marine structure of shipyards; and
  - Decontamination of identified contaminated spots.
- 1.1.4. For the decommissioning of past and existing shipyard lots, there is a total of 39 Marine Lots along the shore of Yau Tong Bay are under the control of the Project Proponent (Main Wealth Development Limited) and covered in this Project. These 39 lots (or the ‘concerned lots’) ,with a total area of over 1 hectare (ha), as listed below and highlighted in **Figure 1**, are hereinafter referred to as the ‘Project Site’. The land uses for the Project Site had been industrial and various land uses including shipyards, timber yards, sawmills and concrete batching plant.
- YTML No. 1
  - YTMLs No. 5-14
  - YTML No. 15
  - YTMLs No. 19-24
  - YTMLs No. 27-38
  - YTMLs No. 41-46
  - YTML No. 54
- 1.1.5. Main Wealth Development Limited (the Project Proponent) has commissioned AECOM Asia Company Limited as the Engineer of the Project and Kin Wing Construction Co., Ltd was commissioned as the Decontamination Contractor of the Project (hereafter referred to as “the Contractor”).
- 1.1.6. AECOM Asia Company Limited was appointed to undertake the Environmental Team (hereafter referred to as “ET”) services for implementation of all the Environmental Monitoring and Audit (hereafter referred to as “EM&A”) works under the Project. Mott MacDonald Hong Kong Limited and Nature & Technologies (HK) Limited act as the Independent Environmental Checker (hereafter referred to as “IEC”) and Independent Environmental Auditor (hereafter referred to as “IEA”) for the Project respectively.
- 1.1.7. According to the updated programme, the demolition works of the Project commenced on 21 November 2011. The demolition works of the building structures on land commenced on 21 November 2011 and was completed in September 2012. The demolition works of marine structures are yet to commence. The remediation method statement was approved by the EPD on 20 December 2013. The soil remediation works commenced on 23 December 2013.
- 1.1.8. In accordance with the updated Environmental Monitoring and Audit Manual (hereinafter referred to as “the EM&A Manual”) of the Project, there is a need of an impact EM&A programme includes daytime construction noise and water quality monitoring, soil remediation works monitoring and auditing and site auditing. The impact EM&A Programme for the Project commenced on 21 November 2011. The EM&A works was suspended from November 2012 for the captioned Project and the EM&A works has been resumed on 28 October 2013.

## 1.2 Scope of Report

- 1.2.1 This is the eighth Quarterly EM&A Summary Report for the Project “Yau Tong Bay – Decommissioning of Shipyard Sites”. This report presents a summary of the environmental monitoring and audit works, list of activities and mitigation measures proposed by the ET for the Project in the quarter between 1 July 2014 and 30 September 2014.

## 1.3 Project Organization

- 1.3.1 The project organization structure is shown in **Appendix A**. The key personnel contact names and numbers are summarized in **Table 1.1**.

**Table 1.1 Contact Information of Key Personnel**

| Party                                                                                      | Name         | Telephone | Fax       |
|--------------------------------------------------------------------------------------------|--------------|-----------|-----------|
| <b>Project Proponent</b><br><br>(Main Wealth Development Limited)                          | Gregory Chan | 2908 8679 | 2562 0029 |
| <b>Engineer</b><br><br>(AECOM Asia Co. Ltd.)                                               | Edward Poon  | 3922 9000 | 3922 9797 |
| <b>Decontamination Contractor (Contractor)</b><br><br>(Kin Wing Construction Co., Ltd)     | Lee Kam Hung | 2717 9139 | 2725 9316 |
| <b>Independent Environmental Checker (IEC)</b><br><br>(Mott MacDonald Hong Kong Limited)   | Terence Kong | 2828 5919 | 2827 1823 |
| <b>Independent Environmental Auditor (IEA)</b><br><br>(Nature & Technologies (HK) Limited) | Gabriel Lam  | 2877 3122 | 2511 0922 |
| <b>Environmental Team Leader (ETL)</b><br><br>(AECOM Asia Co. Ltd.)                        | Y T Tang     | 3922 9393 | 3922 9797 |

#### 1.4 Summary of Construction Works

- 1.4.1 The demolition works of the building structures on land commenced on 21 November 2011 and was completed in September 2012. According to the Project Proponent, the marine structures will not be demolished.
- 1.4.2 As informed by the Contractor, the major construction activities carried out in the reporting quarter were:
- Backfill to Zones R3, R5, R6, R7, R8, A3, A4, T22BA, T22BB, T32C, T32E (inner) and T35C;
  - Cleanup progress monitoring of Biopiles; and
  - Disposal of contaminated soil in Zone T32E to the South East New Territories (SENT) Landfill.
  - Closure Assessment Sampling of Biopile.
- 1.4.3 The general layout plan of the Project site is shown in **Figure 1**.
- 1.4.4 The latest Construction Programme is shown in **Appendix B**.
- 1.4.5 The environmental mitigation measures implementation schedule are presented in **Appendix C**.

## 2 SUMMARY OF EM&A PROGRAMME REQUIREMENTS

### 2.1 Monitoring Parameters and Locations

- 2.1.1 The EM&A Manual designated locations for the monitoring of environmental impacts in terms of construction noise, water quality and land contamination due to the Project.
- 2.1.2 Water quality monitoring will be conducted when the demolition of marine structures commences.
- 2.1.3 The EM&A Manual also requires environmental site inspections for air quality, noise, water quality, waste management, land contamination, and landscape and visual impacts.
- 2.1.4 The description of monitoring parameters, frequencies and durations, and detailed locations of monitoring stations for impact noise are listed below. The monitoring stations for impact noise are depicted in **Figure 2**.

**Table 2.1 Locations of Impact Noise Monitoring Stations**

| Monitoring Station | Location                                        | Description                                                 |
|--------------------|-------------------------------------------------|-------------------------------------------------------------|
| NM1                | Yau Lai Estate<br>Hong Lai House                | 1m from the exterior of the roof top façade of the building |
| NM2                | S.K.H. Yau Tong<br>Kei Hin Primary<br>School    | 1m from the exterior of the roof top façade of the building |
| NM3                | C.C.C. Kei Faat<br>Primary School<br>(Yau Tong) | 1m from the exterior of the roof top façade of the building |

**Table 2.2 Noise Monitoring Parameters, Frequency and Duration**

| Parameter                                                                                                                                    | Frequency                   |
|----------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|
| 30-mins measurement at each monitoring station between 0700 and 1900 on normal weekdays. $L_{eq}$ , $L_{10}$ and $L_{90}$ would be recorded. | At least once per two weeks |

### 2.2 Environmental Quality Performance Limits (Action/Limit Levels)

- 2.2.1 The environmental quality performance limits, i.e. Action and Limit Levels for construction noise monitoring works were derived from the baseline monitoring results as detailed in the EM&A Manual. **Appendix D** shows the established Action and Limit Levels for noise monitoring.

### 2.3 Environmental Mitigation Measures

- 2.3.1 Relevant environmental mitigation measures as recommended in the Project EIA final report were stipulated in the EM&A Manual and environmental requirement in contract documents for the Contractor to adopt. A list of mitigation measures and their implementation statuses, i.e. Implementation Schedule of Environmental Mitigation Measures (EMIS), are given in **Appendix C**.



### 3 NOISE MONITORING

- 3.1.1 Noise monitoring was conducted at 3 designated monitoring stations (NM1 to NM3), for at least once per two weeks during daytime 0700 – 1900 of reporting quarter. The graphical plots of trends of the monitoring results are provided in **Appendix E**.
- 3.1.2 Seven (7) daytime noise monitoring events were carried out at each designated monitoring station (NM1 to NM3) in the reporting quarter.
- 3.1.3 The weather was mostly sunny and fine with occasional cloudy and rainy events in the reporting quarter. Major noise sources during the noise monitoring included construction activities of the Project, construction activities by other contracts and nearby traffic noise.
- 3.1.4 No Action Level exceedance was recorded since no construction noise related complaint was received in the reporting quarter.
- 3.1.5 No Limit Level exceedance was recorded at all monitoring stations in the reporting quarter.
- 3.1.6 **Table 3.1** presents the number of exceedances recorded in each month of the reporting quarter. The number of monitoring events included regular impact monitoring events and additional ones, if any.

**Table 3.1 Summary of Number of Exceedances for Construction Impact Noise Monitoring**

| Monitoring Parameter       | Level of Exceedance                                    | Month    |          |          |          |          |          |          |          |          |
|----------------------------|--------------------------------------------------------|----------|----------|----------|----------|----------|----------|----------|----------|----------|
|                            |                                                        | Jul 14   |          |          | Aug 14   |          |          | Sep 14   |          |          |
|                            |                                                        | NM1      | NM2      | NM3      | NM1      | NM2      | NM3      | NM1      | NM2      | NM3      |
| Daytime Construction Noise | No. of monitoring events                               | 2        | 2        | 2        | 2        | 2        | 2        | 3        | 3        | 3        |
|                            | Action                                                 | 0        | 0        | 0        | 0        | 0        | 0        | 0        | 0        | 0        |
|                            | Limit                                                  | 0        | 0        | 0        | 0        | 0        | 0        | 0        | 0        | 0        |
|                            | <i>Total no. of Action and Limit Level Exceedances</i> | <i>0</i> | <i>0</i> | <i>0</i> | <i>0</i> | <i>0</i> | <i>0</i> | <i>0</i> | <i>0</i> | <i>0</i> |

Remarks: Exceedances which are not project-related are not presented in this table.

## 4 WATER QUALITY MONITORING

- 4.1.1 Water quality monitoring was not conducted in the reporting quarter as the demolition of marine structures has not yet commenced.

## 5 LAND CONTAMINATION MONITORING

### 5.1 Monitoring Status

- 5.1.1 The remediation method statement was approved by the EPD on 20 December 2013. The soil remediation works commenced on 23 December 2013.
- 5.1.2 Cement Solidification and Stabilization was commenced on 21 January 2014 and biopile remediation was commenced on 24 March 2014. Monitoring works has been conducted accordingly. Biopile treatment and Cement Solidification and Stabilization were completed in August 2014 and September 2014 respectively and the treated soil was being used for backfilling.

### 5.2 Excavation Progress

- 5.2.1 As of 30 September 2014, excavation for all contaminated soil requiring biopile and/or cement solidification treatment has been completed in zones T19A, T22BA, T22BB, T32C, T32E, T35C, T36A, A1, A2, A3, A4, A5, R1, R2, R3, R4, R5, R6, R7 and R8. Soil in zone T32D, which required landfill disposal, has not been excavated yet and will be excavated in later phase.
- 5.2.2 Verification sampling has been conducted according to the corresponding CAR/RAPs ((a) *Appendix 7C – Remediation Action Plan for Yau Tong Bay Marine Lots in the Reclamation of Yau Tong Bay Final EIA Report (January 2002)*; (b) *Yau Tong Bay - Decommissioning of Shipyard Sites - Contamination Assessment Report and Remediation Action Plan (YTML 1, 6-11, 15, 28, 29, 38 and 41-43*; (c) *Yau Tong Bay – Decommissioning of Shipyard Sites - Supplementary Contamination Assessment Report and Remediation Action Plan for Previously Inaccessible Lots (YTML 27, 44, 45-46, 54 and Underground Oil Tank at YTML 6-11)*) to define the contamination extent. The excavation extends for all the zones have been confirmed in May, according to the verification sampling results. The locations of the contamination zones are shown in **Figure 4** and the finalized excavation extent of the contaminated zones are indicated in **Figures 5 to 12**.

### 5.3 Biopiling and Cement Solidification / Stabilization Progress

- 5.3.1 The set up of the biopiling facility has been completed and treatment has been commenced in March. Excavated soil from Zones A2, R1, R2, R3, R4, T32E(outer) and T35C has been transferred to the facility. Biopilling treatment was in progress during the reporting quarter and progress monitoring samples were collected regularly to check if remediation targets have been achieved. As of 30 September 2014, biopiling treatment for all samples were completed.
- 5.3.2 Cement Solidification / Stabilization have been conducted for contaminated soil from zones A2 and T32E. 10 monitoring samples of the cement-treated soil were collected for Toxicity Characteristic Leaching Procedure (TCLP) and Unconfined Compressive Strength (UCS) tests in the reporting quarter. The tested results showed that the remediation targets were achieved for all samples.

### 5.4 Landfill Disposal Progress

- 5.4.1 Contaminated soil in zone T32D and a portion of zone T32E (T32E(inner)) is subjected to be disposed at landfill. The soils are packed and sealed in impermeable containers with proper labels. The containers with the contaminated soil are then collected and transferred from the Site to the South East New Territories (SENT) Landfill by a licensed chemical waste collector, Sun Base Environmental Service Limited. In total, 191,250 kg (approximately 126m<sup>3</sup>) of contaminated soil has been transported to SENT in the reporting period.

## **5.5 IEA Spot Check Samples**

- 5.5.1 The Independent Environmental Auditor (IEA) conducted spot check sampling on 7 July 2014, 25 July 2014 and 15 August 2014. A total of 3 spot check samples were collected from July to September 2014. The results of the spot check samples are in order with the Contractor's samples.

## **6 ENVIRONMENTAL SITE INSPECTION AND AUDIT**

6.1.1 There were thirteen (13) site inspections (including three (3) ET, IEC and IEA joint site inspections) conducted in the reporting quarter. The joint site inspections were conducted on 23 July 2014, 25 August 2014 and 25 September 2014.

6.1.2 The environmental site inspections and audits are to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. The major concerns for the Project are air quality, noise, water quality, and chemical and waste management. Observations recorded are described below.

6.1.3 The Contractor has partially rectified observations as identified during environmental site inspections in the reporting quarter within the agreed time frame. Rectifications of remaining identified items are undergoing by the Contractor. Follow-up inspections on the status on provision of mitigation measures will be conducted to ensure all identified items are mitigated properly.

### **Air Quality**

6.1.4 Regular spraying of water has been maintained for areas not covered by water sprinklers. (Reminder)

6.1.5 The stockpile of bioremediated soil has been transferred for backfilling or cement S/S. The impervious sheet has been temporarily removed during the transferring process.

6.1.6 Since the cement for solidification process was mixed with soil and water once it is debagged, the dust generated in de-begging and mixing process has been minimised.

### **Noise**

6.1.7 A few hoardings at the seawall side were found temporary removed. The Contractor was reminded to maintain the condition of the hoarding as per the approved hoarding plan. Also, temporary measures such as barricades and sand bags shall be provided in order to prevent surface run-off being discharged outside the site boundary. (Reminder)

### **Water Quality**

6.1.8 No adverse observation was identified in the reporting quarter.

### **Land Contamination**

6.1.9 IEA has collected spot check samples and the results are in order with the verification samples collected by the Contractor.

### **Chemical and Waste Management**

6.1.10 The contaminated soil to be disposed of to the landfill (as chemical wastes) is filled in labelled drums or bags, and temporary stored inside a truck's tank provided by a licensed chemical waste collector. The chemical waste collector then collects the tank and disposes of the contaminated soil to the landfill at a regular time interval (Reminder).

### **Landscape and Visual Impact**

6.1.11 No adverse observation was identified in the reporting quarter.

### **Miscellaneous**

6.1.12 No adverse observation was identified in the reporting quarter.

## 7 ADVICE ON SOLID AND LIQUID WASTE MANAGEMENT STATUS

- 7.1.1 The Contractor submitted the application form for registration as a chemical waste producer for the Project.
- 7.1.2 As advised by the Contractor, 0m<sup>3</sup> of soil (of which 0m<sup>3</sup> was artificial hard material) was excavated on site; it will be either mixed with cement or transferred to biopile for treatment. No general refuse was generated on site and disposed of at the SENT Landfill. 0m<sup>3</sup> of inert C&D materials were reused on site. 135m<sup>3</sup> of excavated soil was disposed of at the SENT Landfill. No metals, paper/cardboard packaging or plastics were generated and collected by the registered recycling collectors.
- 7.1.3 The Contractor is advised to properly maintain on site C&D material and waste sorting, and collection and recording system, and maximize the reuse / recycling of C&D materials and wastes. The Contractor is reminded to properly maintain the site tidiness and dispose of wastes accumulated on site regularly and properly.

## 8 SUMMARY OF NON-COMPLIANCE (EXCEEDANCES) OF ENVIRONMENTAL QUALITY PERFORMANCE LIMITS (ACTION AND LIMIT LEVELS)

- 8.1.1 No Action Level exceedance was recorded since no construction noise related complaint was received in the reporting quarter.
- 8.1.2 No Limit Level exceedance of construction noise was recorded in the reporting quarter.
- 8.1.3 Water quality monitoring was not conducted in the reporting quarter as demolition of marine structures was not commenced.

## 9 COMPLAINT, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTION

- 9.1.1 The Environmental Complaint Handling Procedure is annexed in **Figure 3**.
- 9.1.2 No environmental complaint, notification of summons and successful prosecution was received in the reporting quarter.
- 9.1.3 Table 9.1 summarizes the numbers of complaints, summons and successful prosecutions received in the reporting quarter.

**Table 9.1 Summary of Environmental Complaints, Summons and Successful Prosecutions**

|                         | Apr 14 | May 14 | Jun 14 | Total |
|-------------------------|--------|--------|--------|-------|
| Complaints              | 0      | 0      | 0      | 0     |
| Summons                 | 0      | 0      | 0      | 0     |
| Successful Prosecutions | 0      | 0      | 0      | 0     |

- 9.1.4 Statistics on complaints, notifications of summons and successful prosecutions recorded in the reporting quarter and since the commencement of the Project are given in **Appendix F**.

## **10 COMMENTS, RECOMMENDATIONS AND CONCLUSIONS**

### **10.1 Comments on Mitigation Measures**

10.1.1 According to the environmental site inspections performed in the reporting quarter, the following comments are provided:

#### **Air Quality**

10.1.2 Regular spraying of water has been maintained for areas not covered by water sprinklers.

10.1.3 The stockpile of bioremediated soil has been transferred for backfilling or cement S/S. The impervious sheet should be put back after the transferring process.

10.1.4 Since the cement for solidification process was mixed with soil and water once it is debagged, the dust generated in de-begging and mixing process should be minimised.

#### **Noise**

10.1.5 The Contractor was reminded to maintain the condition of the hoarding as per the approved hoarding plan. Also, temporary measures such as barricades and sand bags shall be provided in order to prevent surface run-off being discharged outside the site boundary.

#### **Water Quality**

10.1.6 Nil.

#### **Land Contamination**

10.1.7 Nil.

#### **Chemical and Waste Management**

10.1.8 The contaminated soil to be disposed of to the landfill (as chemical wastes) is filled in labelled drums or bags, and temporary stored inside a truck's tank provided by a licensed chemical waste collector. The chemical waste collector then collects the tank and disposes of the contaminated soil to the landfill at a regular time interval.

#### **Landscape and Visual Impact**

10.1.9 Nil.

#### **Miscellaneous**

10.1.10 Nil.

### **10.2 Recommendations on EM&A Programme**

10.2.1 The impact noise and water quality monitoring programme ensured that any environmental impact to the receivers would be readily detected and timely actions could be taken to rectify any non-compliance. Assessment and analysis of monitoring results collected demonstrated the environmental acceptability of the Project. The weekly site inspection and soil remediation monitoring and auditing ensured that all the environmental mitigation measures recommended in the EIA report were effectively implemented.

10.2.2 The EM&A programme effectively monitored the environmental impacts from the construction activities and no particular recommendation was advised for the improvement of the programme.

### **10.3 Conclusions**

- 10.3.1 Noise monitoring was carried out 7 times from 1 July 2014 to 30 September 2014, in accordance with the EM&A Manual.
- 10.3.2 No Action Level exceedance was recorded since no construction noise related complaint was received in the reporting quarter.
- 10.3.3 No Limit Level exceedance of construction noise was recorded in the reporting quarter.
- 10.3.4 Water quality monitoring was not conducted in the reporting quarter as the demolition of marine structures has not yet commenced.
- 10.3.5 As informed by the Contractor, the major construction activities carried out in the reporting quarter were:
- Backfill to Zones R3, R5, R6, R7, R8, A3, A4, T22BA, T22BB, T32C, T32E (inner) and T35C;
  - Cleanup progress monitoring of Biopiles; and
  - Disposal of contaminated soil in Zone T32E to the South East New Territories (SENT) Landfill.
  - Closure Assessment Sampling of Biopile.
- 10.3.6 Environmental site inspection was carried out 13 times in the reporting quarter. Recommendations on remedial actions were given to the Contractor for the deficiencies identified during the site audits.
- 10.3.7 No environmental complaint, notification of summons and successful prosecution was received in the reporting quarter.

---


---

## FIGURES

---

---



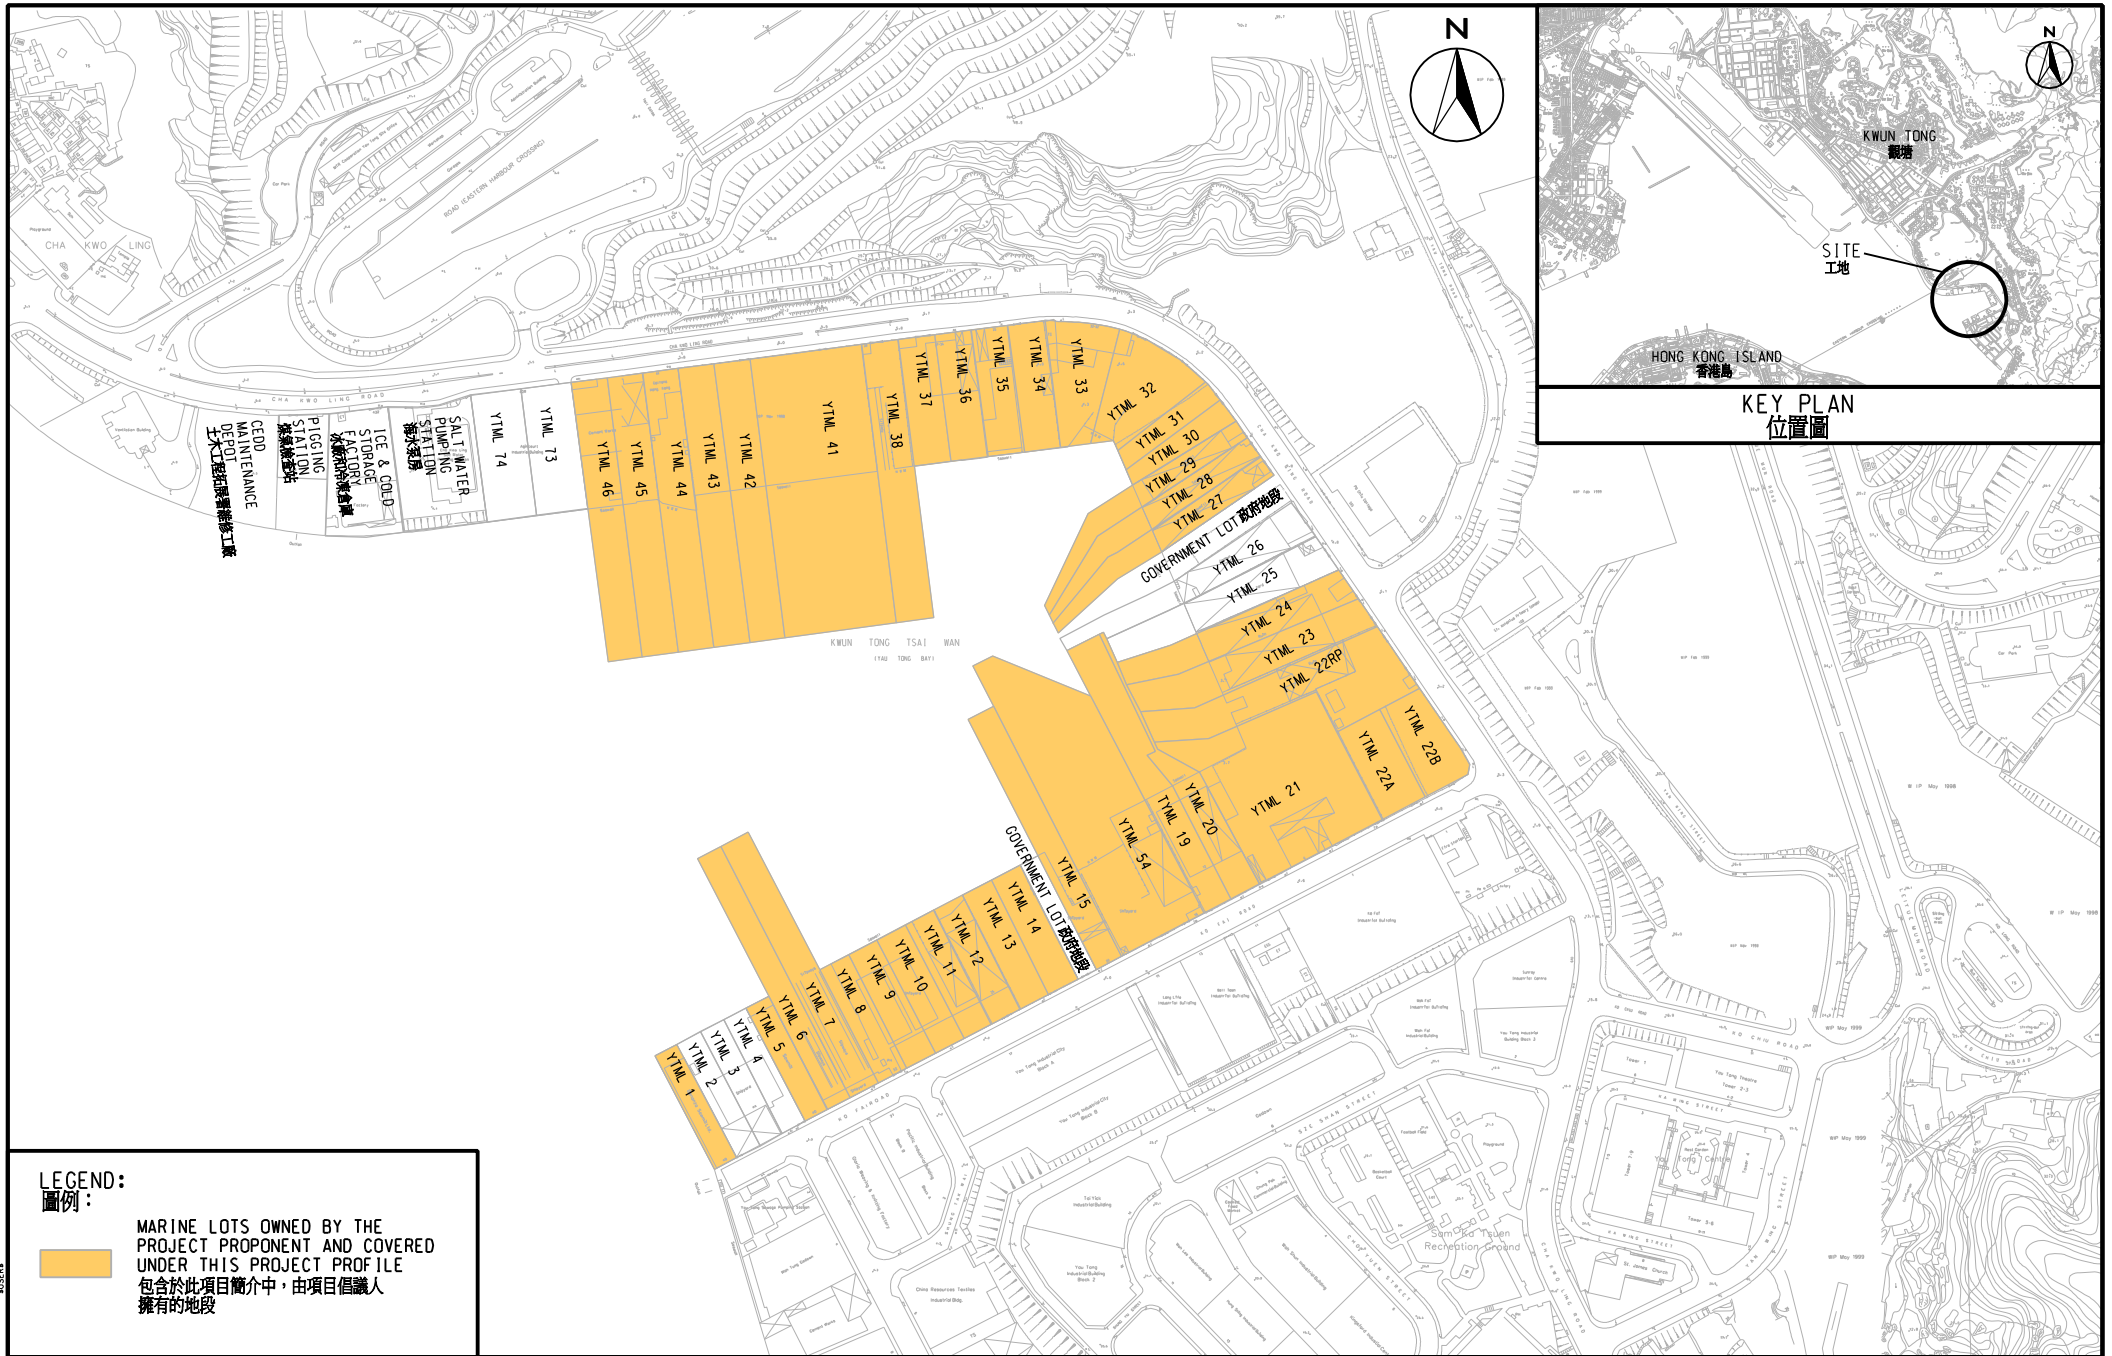

**LEGEND:**  
**圖例:**

MARINE LOTS OWNED BY THE PROJECT PROPONENT AND COVERED UNDER THIS PROJECT PROFILE  
 包含於此項目簡介中，由項目倡議人擁有的地段


YAU TONG BAY – DECOMMISSIONING OF SHIPYARD SITES PROJECT PROFILE

油蔴地 - 船廠拆卸工程

**SITE LOCATION PLAN**  
**工地位置圖**

|             |             |             |          |          |
|-------------|-------------|-------------|----------|----------|
| SCALE<br>比例 | A4 1 : 4500 | DATE<br>日期  | NOV 2010 |          |
| CHECK<br>校對 | --          | DRAWN<br>繪圖 | --       |          |
| JOB No.     | 60048283    | FIGURE No.  | 1        | REV<br>A |

PLOTING BY: SATEK

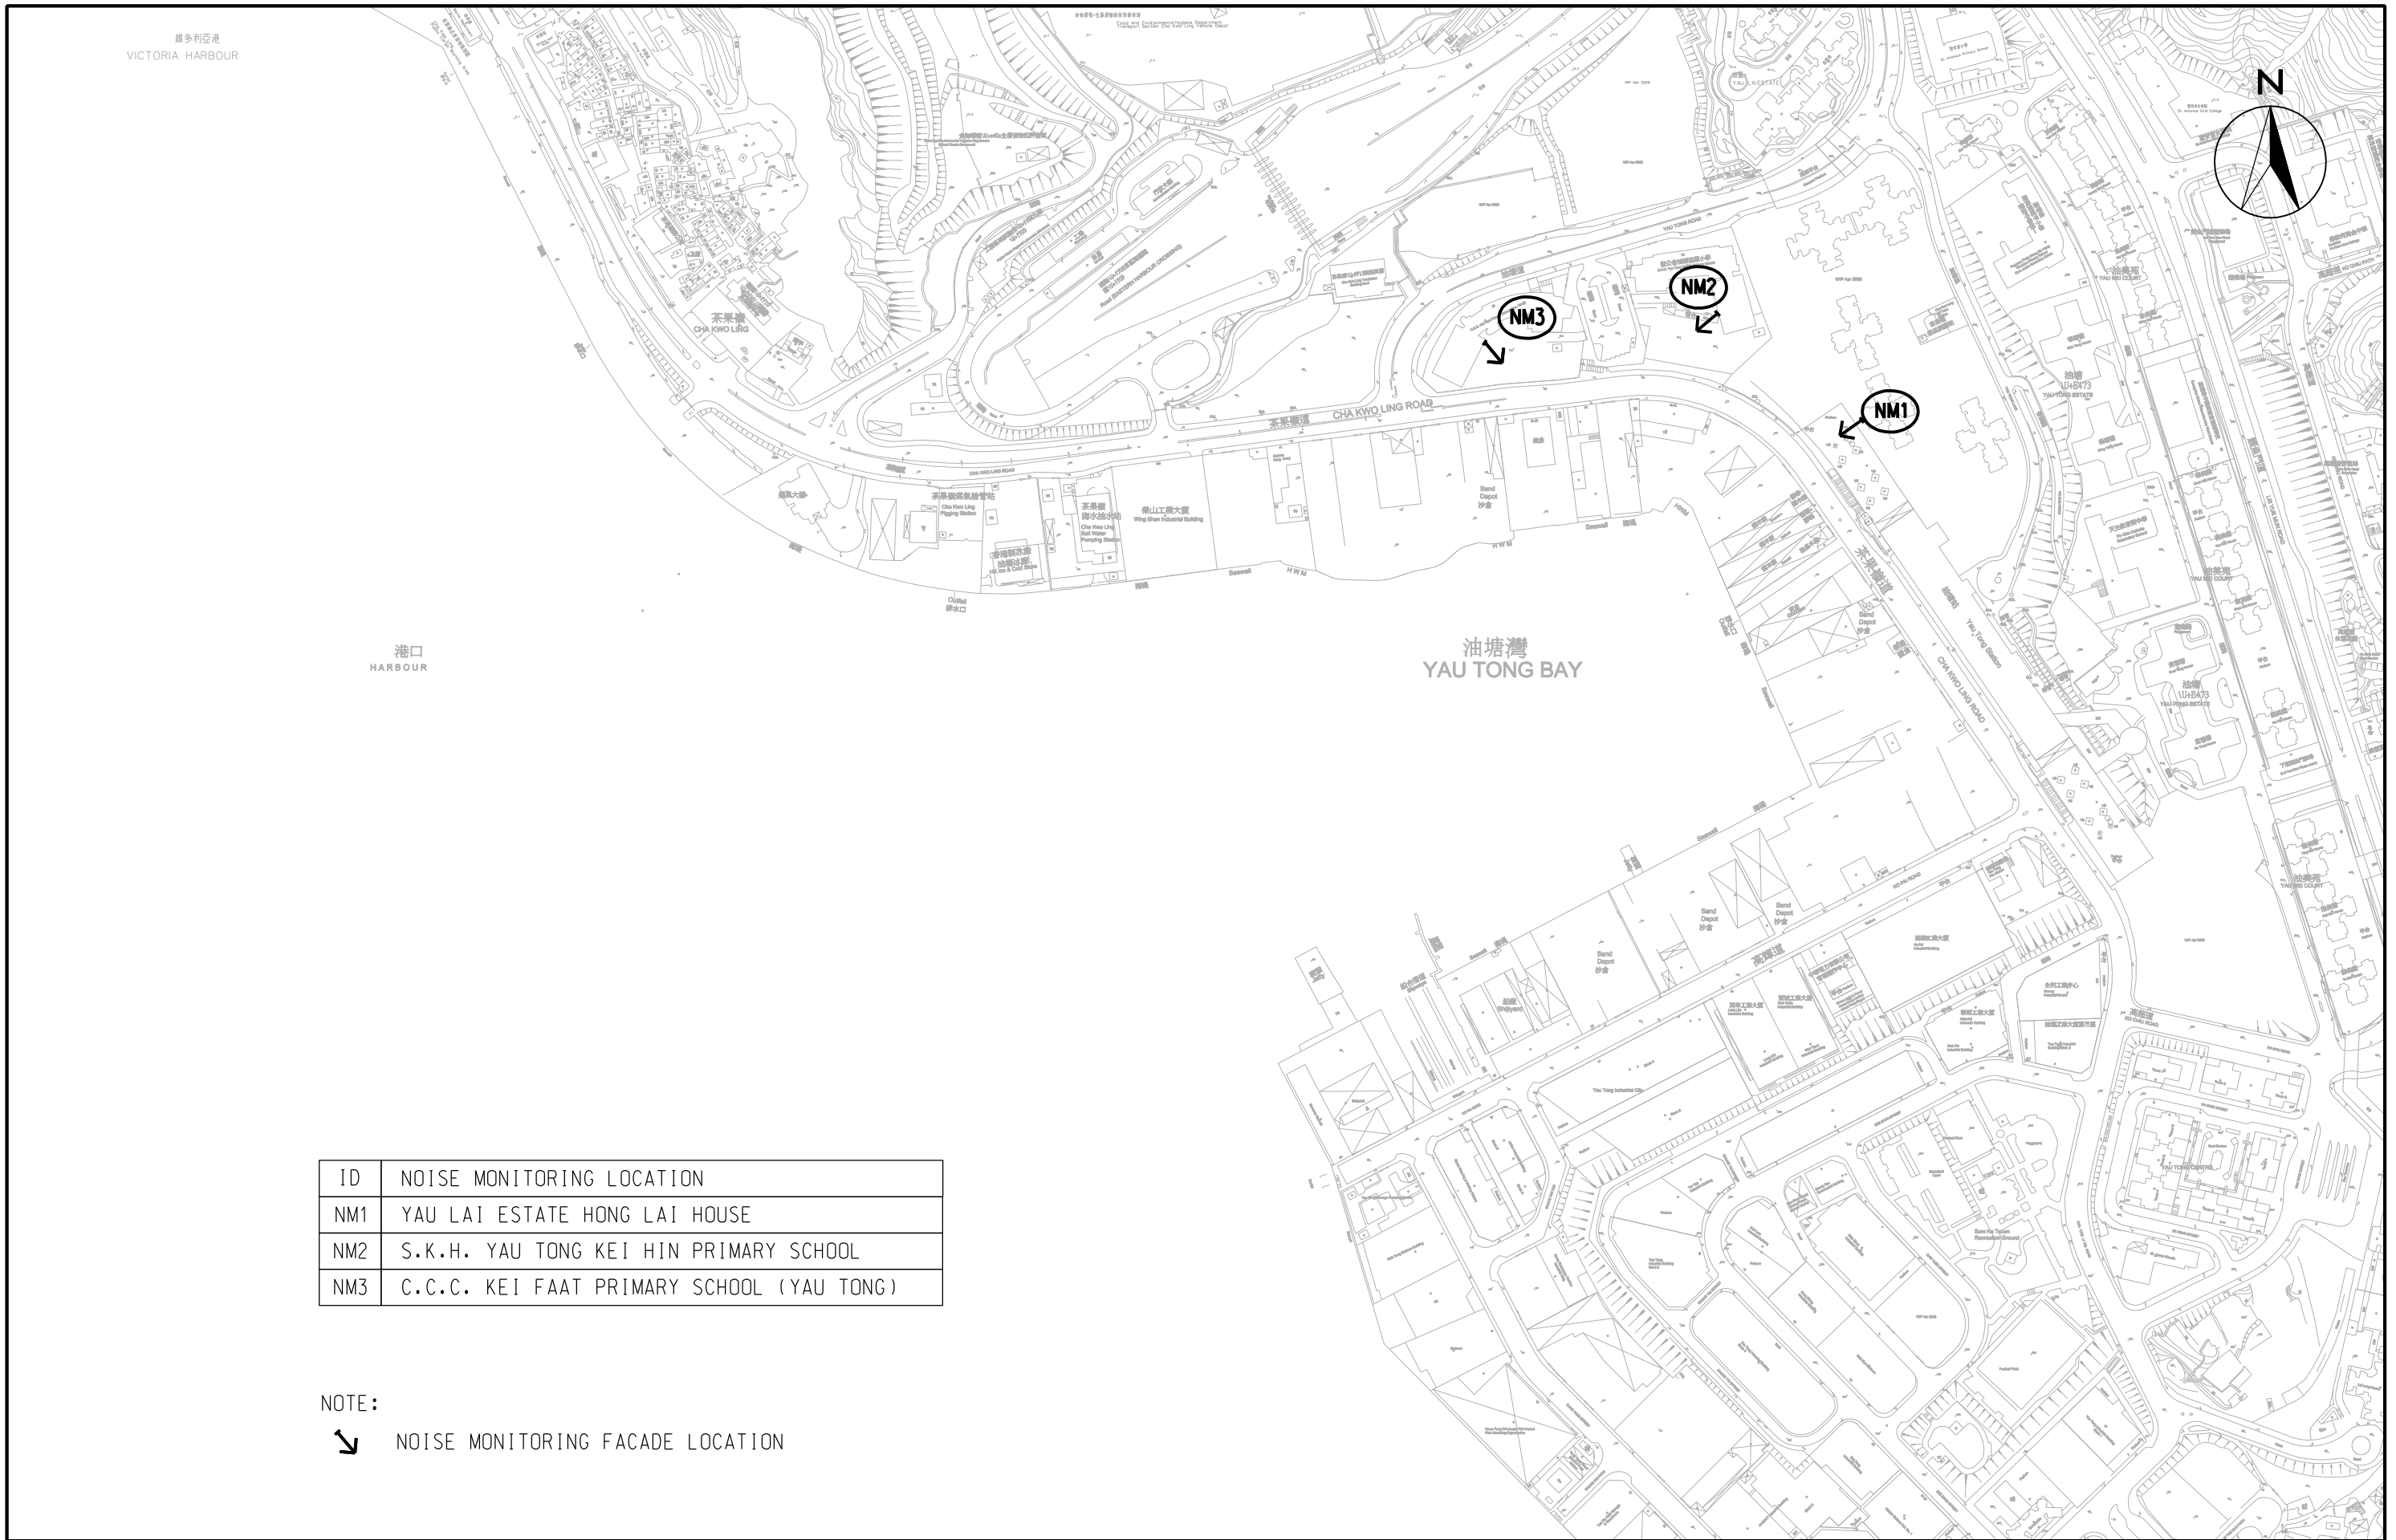

| ID  | NOISE MONITORING LOCATION                 |
|-----|-------------------------------------------|
| NM1 | YAU LAI ESTATE HONG LAI HOUSE             |
| NM2 | S.K.H. YAU TONG KEI HIN PRIMARY SCHOOL    |
| NM3 | C.C.C. KEI FAAT PRIMARY SCHOOL (YAU TONG) |

NOTE:


↙ NOISE MONITORING FACADE LOCATION

YAU TONG BAY - DECOMMISSIONING OF SHIPYARD SITES

NOISE MONITORING LOCATIONS


**AECOM**

|             |             |            |           |        |
|-------------|-------------|------------|-----------|--------|
| SCALE       | A3 1 : 3000 | DATE       | AUG. 2011 |        |
| CHECK       | LSHT        | DRAWN      | LLHY      |        |
| PROJECT NO. | 60048283    | FIGURE NO. | 2         | REV -- |

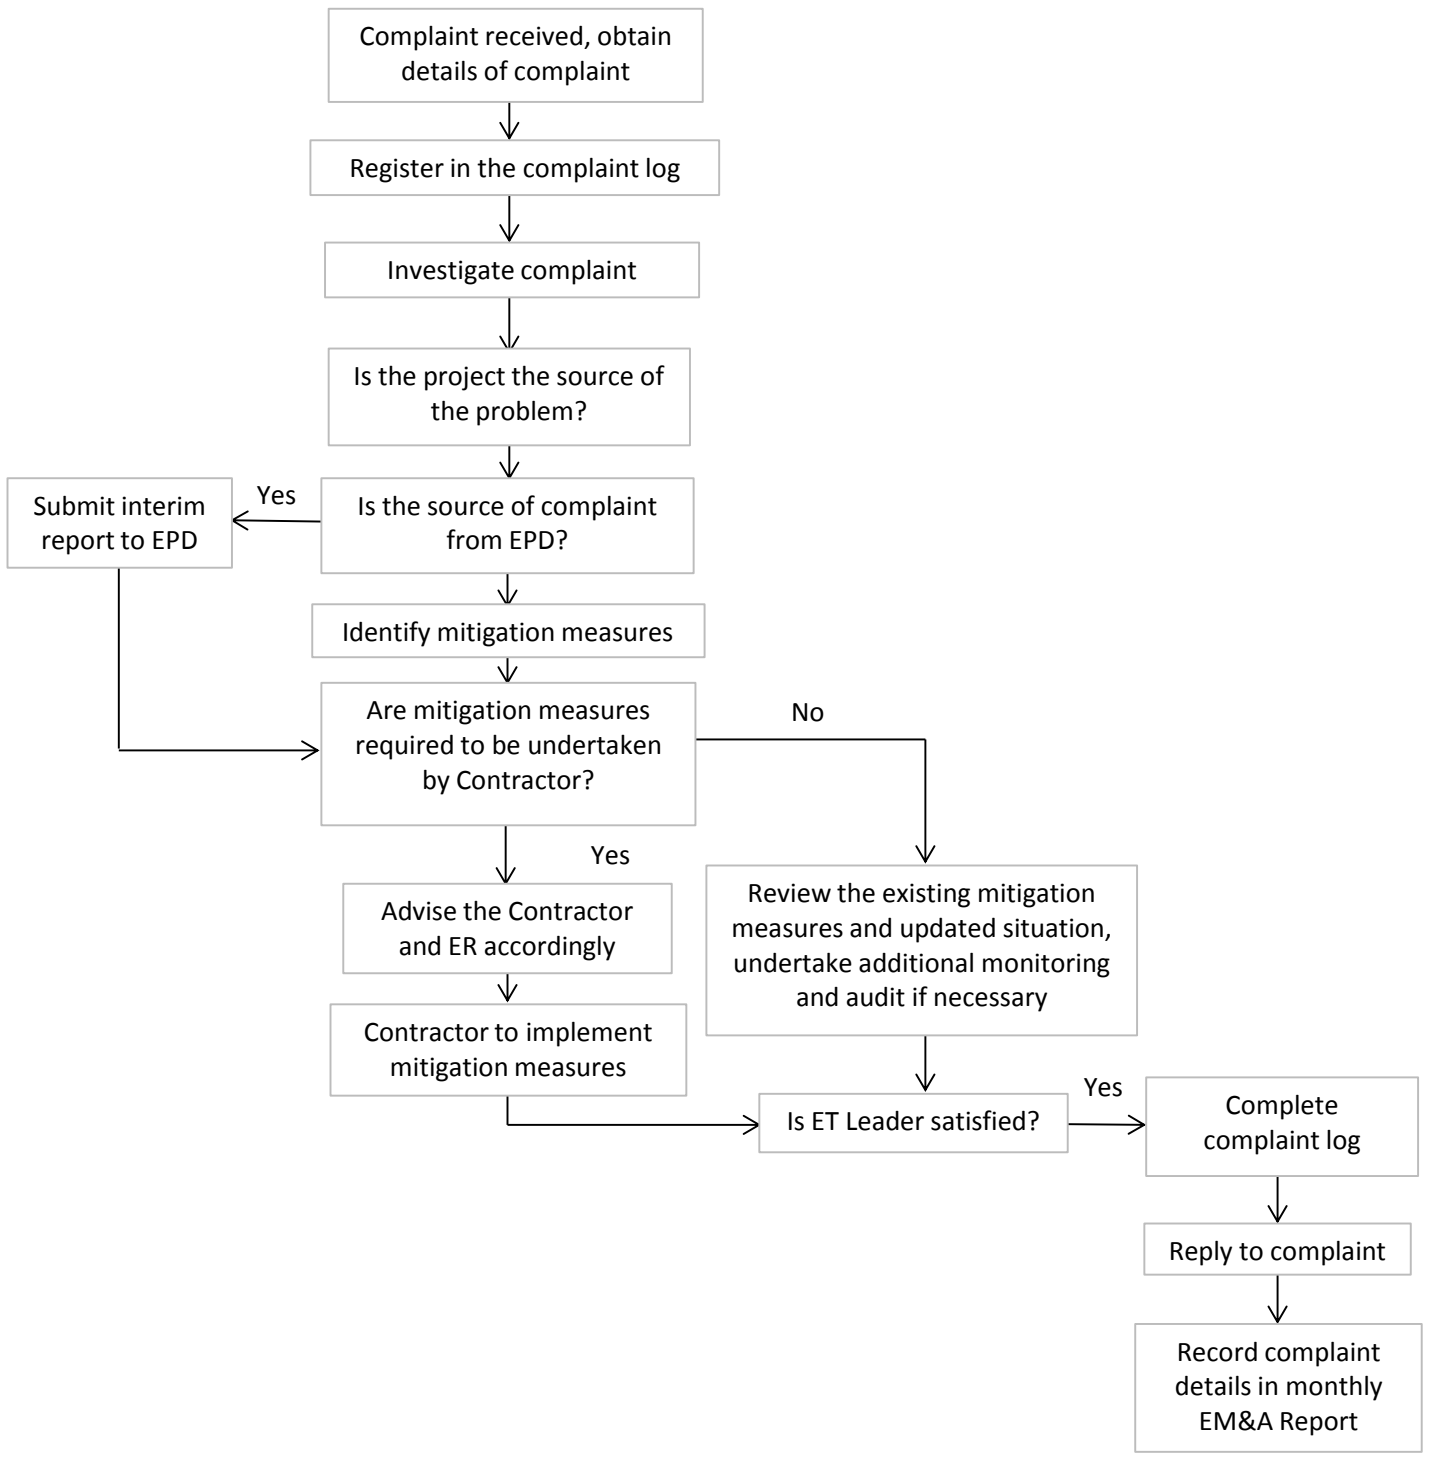

|              |                                                         |         |          |            |        |
|--------------|---------------------------------------------------------|---------|----------|------------|--------|
| <b>AECOM</b> | <b>Yau Tong Bay – Decommissioning of Shipyard Sites</b> | SCALE   | N.T.S.   | DATE       | Dec-11 |
|              |                                                         | CHECK   | ENFL     | DRAWN      | JWYM   |
|              | Environmental Complaint Handling Procedure              | JOB NO. | 60048283 | FIGURE NO. | 3      |





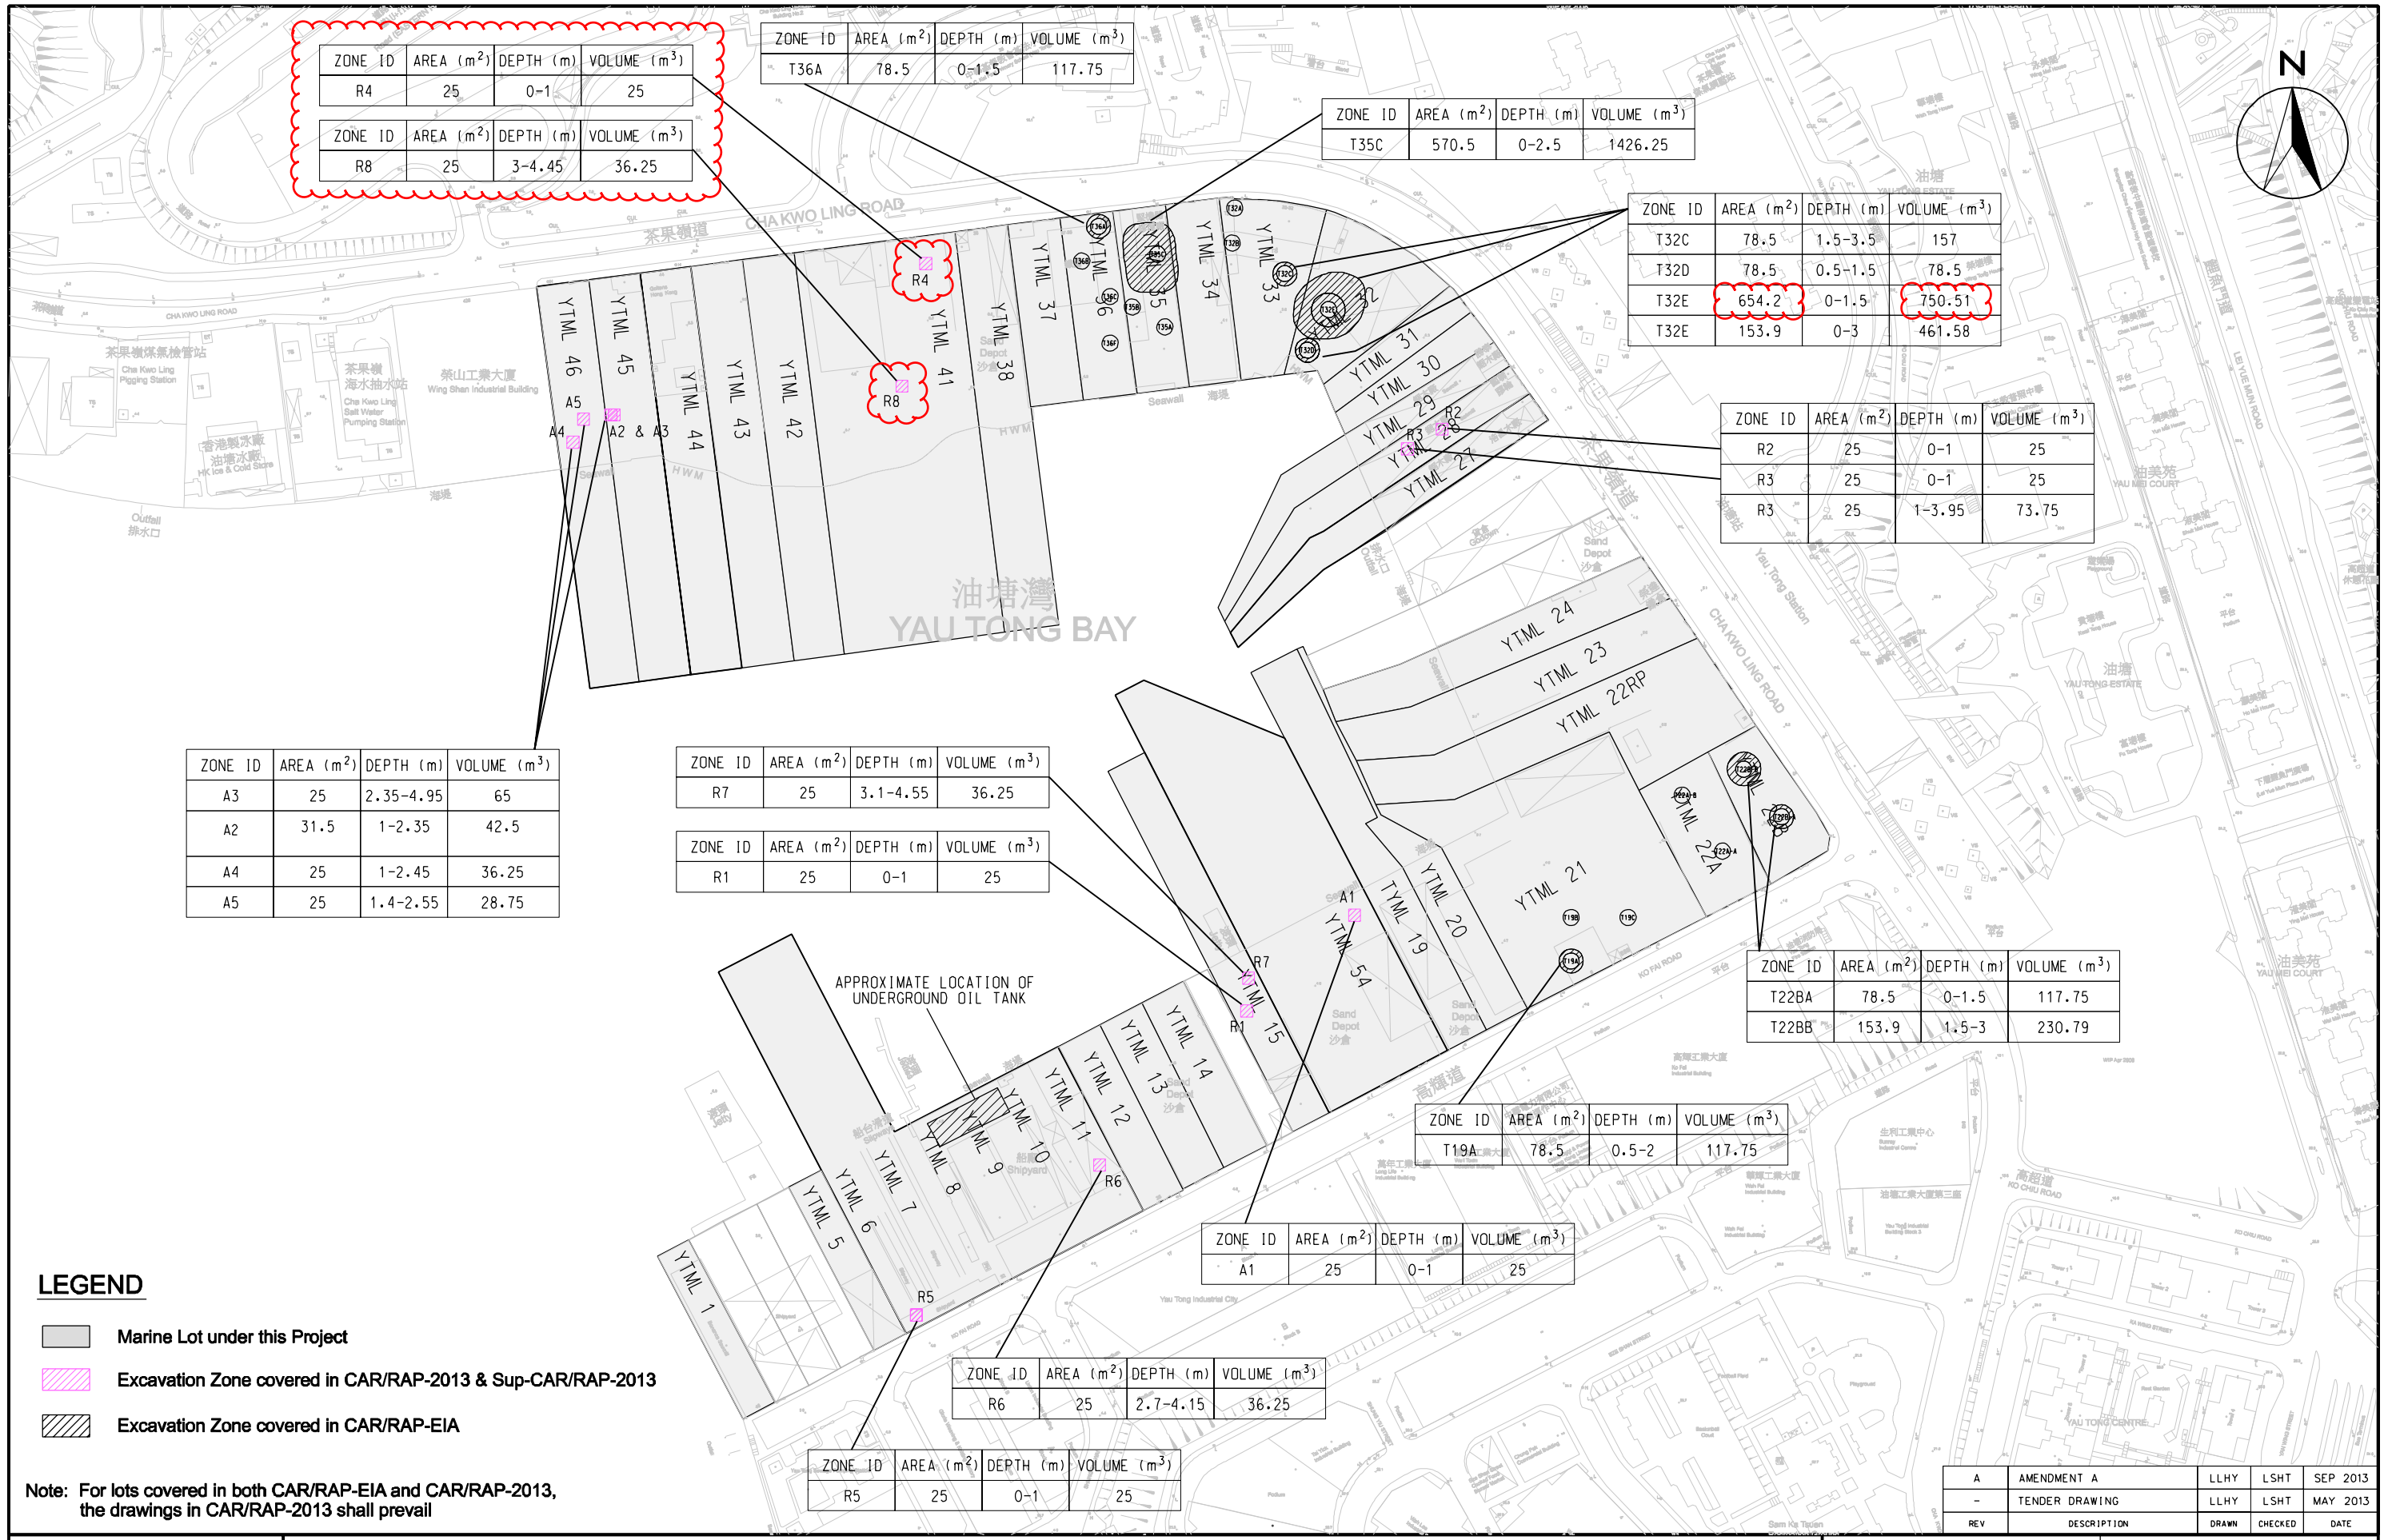

# LOCATIONS OF CONTAMINATED ZONES

|             |           |            |          |
|-------------|-----------|------------|----------|
| SCALE       | A3 1:2500 | DATE       | MAY 2013 |
| CHECK       | LSHT      | DRAWN      | LLHY     |
| PROJECT NO. | 60048208  | FIGURE NO. | 4        |

| ZONE | DEPTH WITH CONTAMINATED SOIL FOUND (m BELOW GROUND SURFACE) | CONTAMINANT IDENTIFIED | ESTIMATED EXTENT OF CONTAMINATION (m <sup>2</sup> ) | VOLUME (m <sup>3</sup> ) | PROPOSED REMEDIATION METHOD    |
|------|-------------------------------------------------------------|------------------------|-----------------------------------------------------|--------------------------|--------------------------------|
| R5   | 0-1.0m                                                      | LEAD                   | 25                                                  | 25                       | SOLIDIFICATION / STABILIZATION |
| R6   | 2.7-4.15m                                                   | LEAD                   | 25                                                  | 36.25                    | SOLIDIFICATION / STABILIZATION |

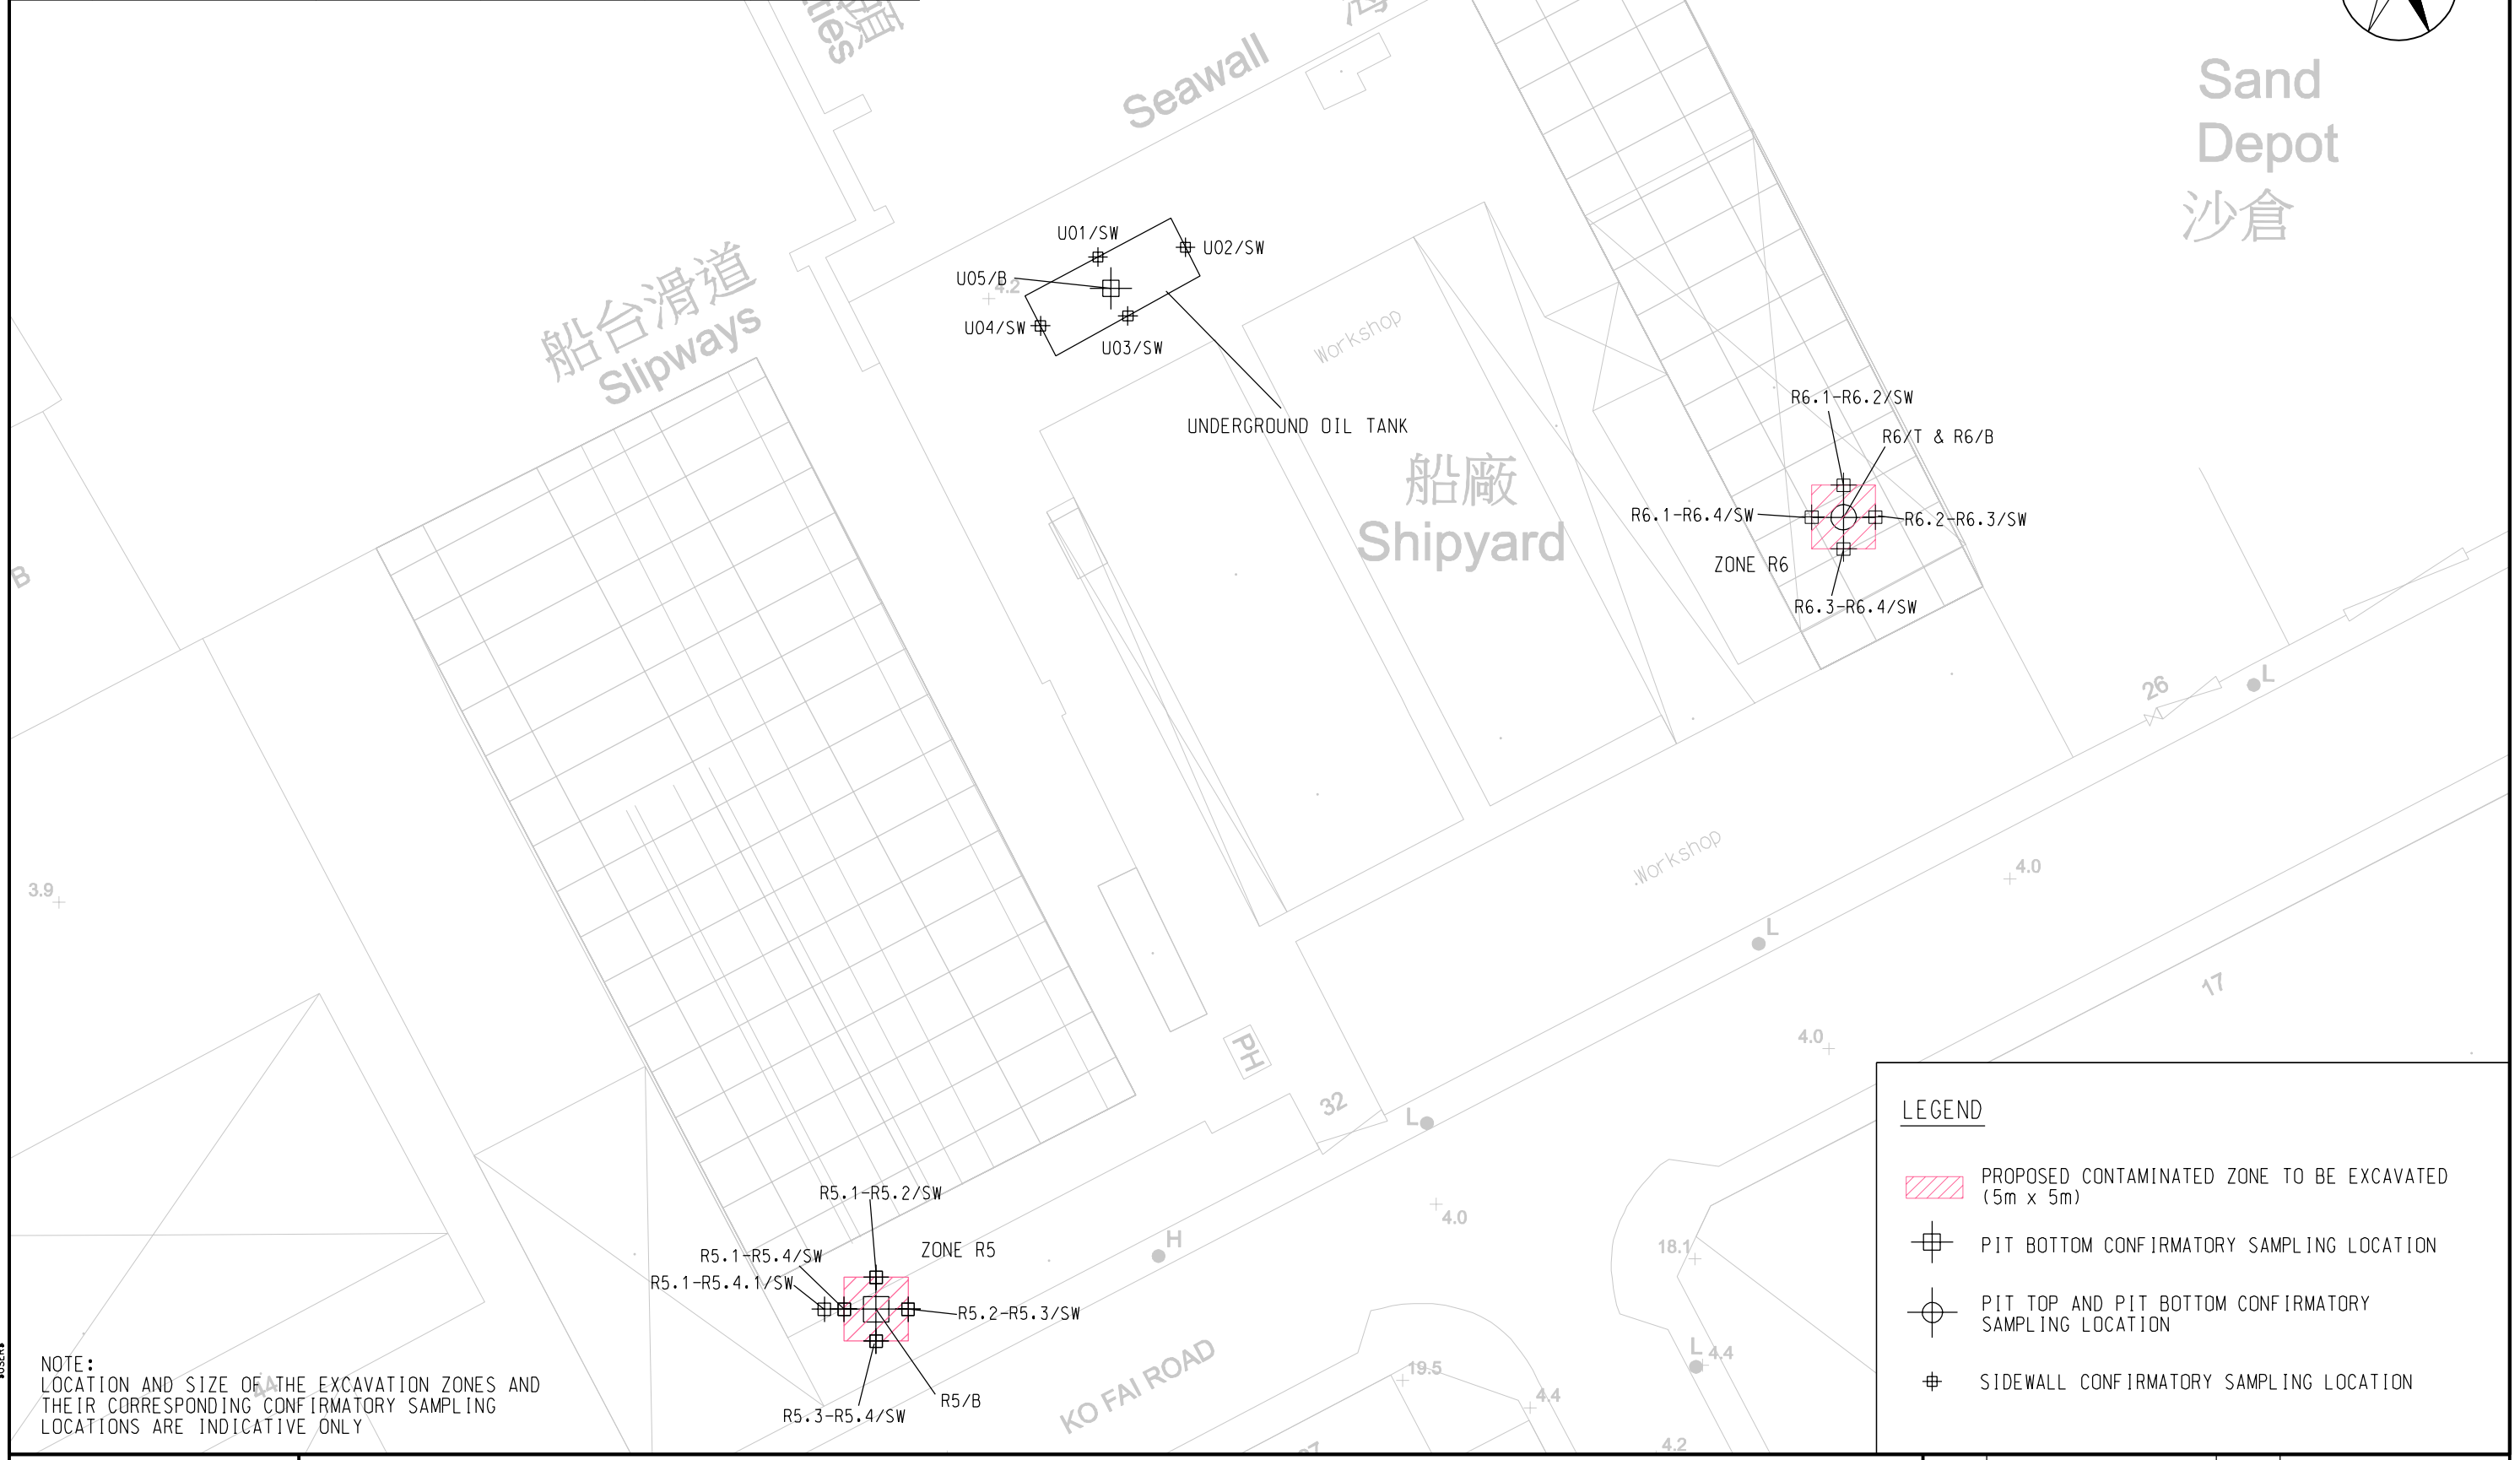

| LEGEND |                                                       |
|--------|-------------------------------------------------------|
|        | PROPOSED CONTAMINATED ZONE TO BE EXCAVATED (5m x 5m)  |
|        | PIT BOTTOM CONFIRMATORY SAMPLING LOCATION             |
|        | PIT TOP AND PIT BOTTOM CONFIRMATORY SAMPLING LOCATION |
|        | SIDEWALL CONFIRMATORY SAMPLING LOCATION               |

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND THEIR CORRESPONDING CONFIRMATORY SAMPLING LOCATIONS ARE INDICATIVE ONLY


YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS

LOCATION OF CONFIRMATORY SAMPLING (ZONES R5 & R6)




|         |            |             |          |
|---------|------------|-------------|----------|
| SCALE   | A3 1 : 500 | DATE        | APR 2014 |
| CHECK   | LLHY       | DRAWN       | KW       |
| JOB No. | 60048208   | DRAWING No. | 5        |
|         |            | REV         | -        |

Plotting By: DATES



| ZONE | DEPTH WITH CONTAMINATED SOIL FOUND (m BELOW GROUND SURFACE) | CONTAMINANT IDENTIFIED       | ESTIMATED EXTENT OF CONTAMINATION (m <sup>2</sup> ) | VOLUME (m <sup>3</sup> ) | PROPOSED REMEDIATION METHOD    |
|------|-------------------------------------------------------------|------------------------------|-----------------------------------------------------|--------------------------|--------------------------------|
| R1   | 0-1.0m                                                      | BIS-(2-ETHYLHEXYL)-PHTHALATE | 25                                                  | 25                       | BIOPILING                      |
| R7   | 3.1-4.55m                                                   | LEAD                         | 25                                                  | 36.25                    | SOLIDIFICATION / STABILIZATION |

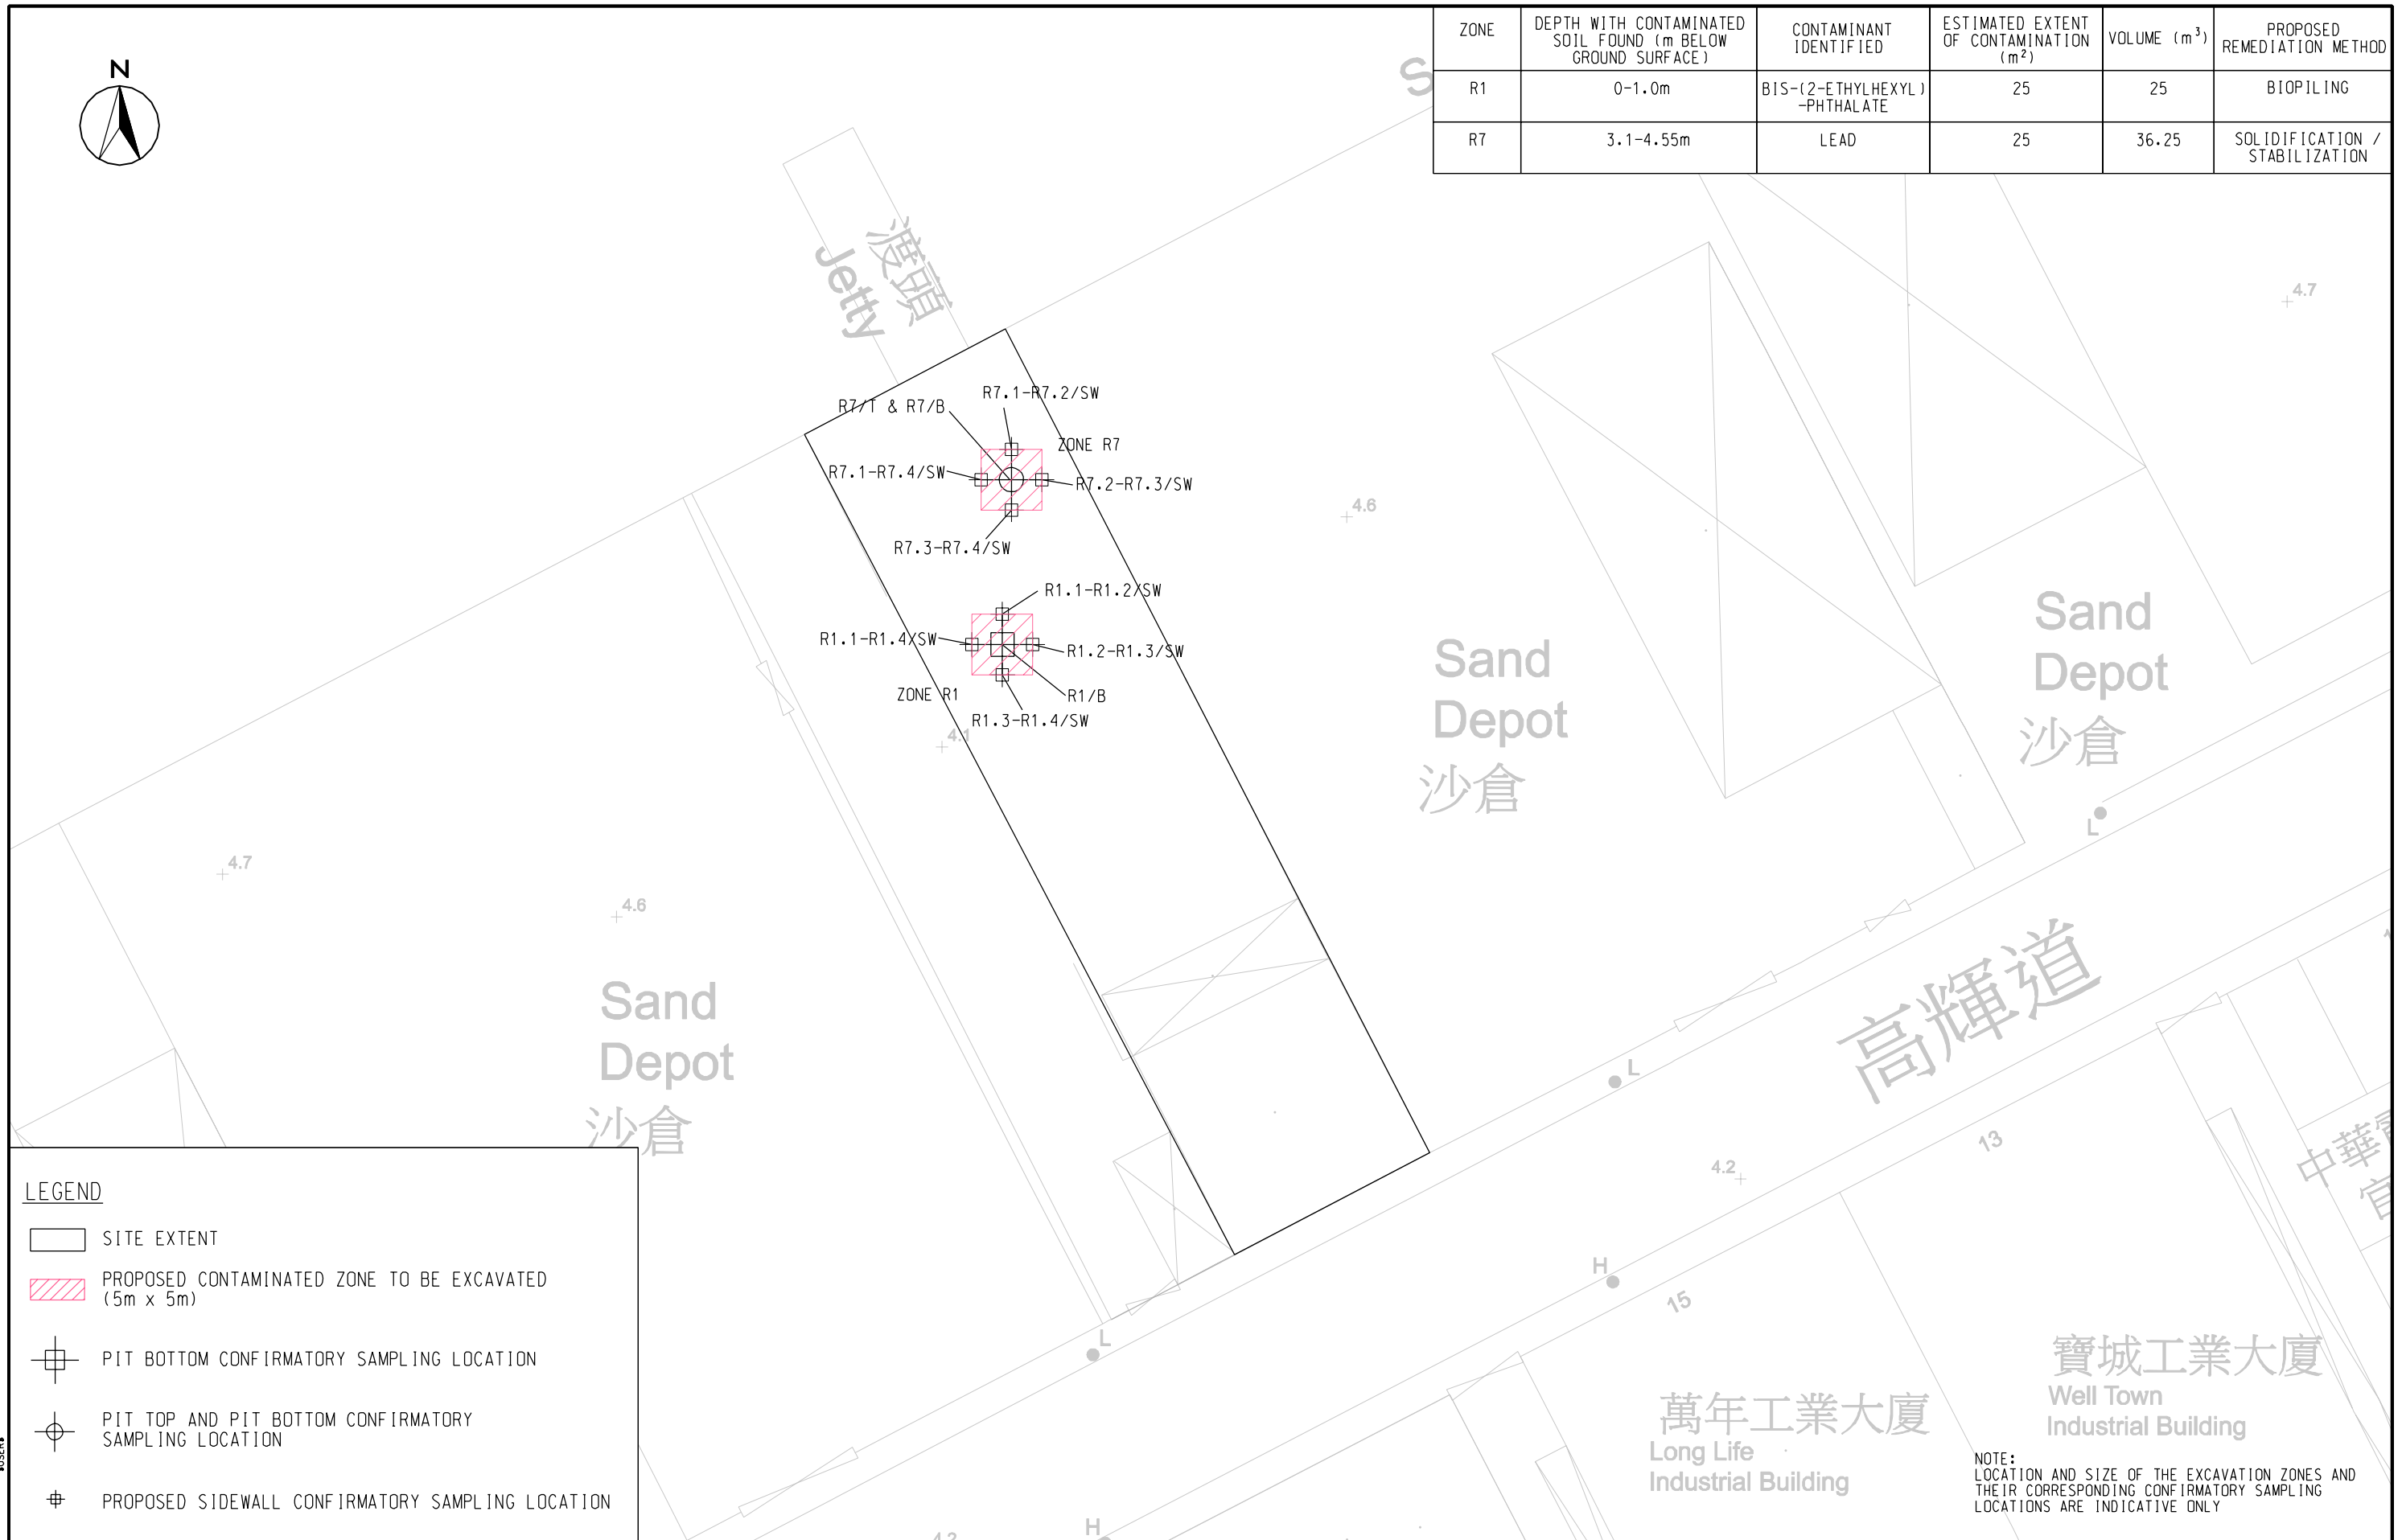

**LEGEND**

- SITE EXTENT
- PROPOSED CONTAMINATED ZONE TO BE EXCAVATED (5m x 5m)
- + PIT BOTTOM CONFIRMATORY SAMPLING LOCATION
- ⊕ PIT TOP AND PIT BOTTOM CONFIRMATORY SAMPLING LOCATION
- ⊞ PROPOSED SIDEWALL CONFIRMATORY SAMPLING LOCATION

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND THEIR CORRESPONDING CONFIRMATORY SAMPLING LOCATIONS ARE INDICATIVE ONLY

YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS



LOCATION OF CONFIRMATORY SAMPLING (ZONES R1 & R7)



|         |            |             |          |
|---------|------------|-------------|----------|
| SCALE   | A3 1 : 500 | DATE        | JAN 2014 |
| CHECK   | LLHY       | DRAWN       | KW       |
| JOB No. | 60048208   | DRAWING No. | 6        |
|         |            | REV         | -        |



| ZONE | DEPTH WITH CONTAMINATED SOIL FOUND (m BELOW GROUND SURFACE) | CONTAMINANT IDENTIFIED       | ESTIMATED EXTENT OF CONTAMINATION (m <sup>2</sup> ) | VOLUME (m <sup>3</sup> ) | PROPOSED REMEDIATION METHOD |
|------|-------------------------------------------------------------|------------------------------|-----------------------------------------------------|--------------------------|-----------------------------|
| R2   | 0-1.0m                                                      | BIS-(2-ETHYLHEXYL)-PHTHALATE | 25                                                  | 25                       | BIOPILING                   |
| R3   | 0-1.0m                                                      | BIS-(2-ETHYLHEXYL)-PHTHALATE | 25                                                  | 25                       | BIOPILING                   |
|      | 1.0-3.95m                                                   | PCR (C17 - C35)              | 25                                                  | 73.75                    | BIOPILING                   |
|      | 2.5-3.95m                                                   | PCR (C9 - C16)               | 25                                                  | 36.25                    | BIOPILING                   |
|      | 2.5-3.95M                                                   | BENZENE                      | 25                                                  | 36.25                    | BIOPILING                   |

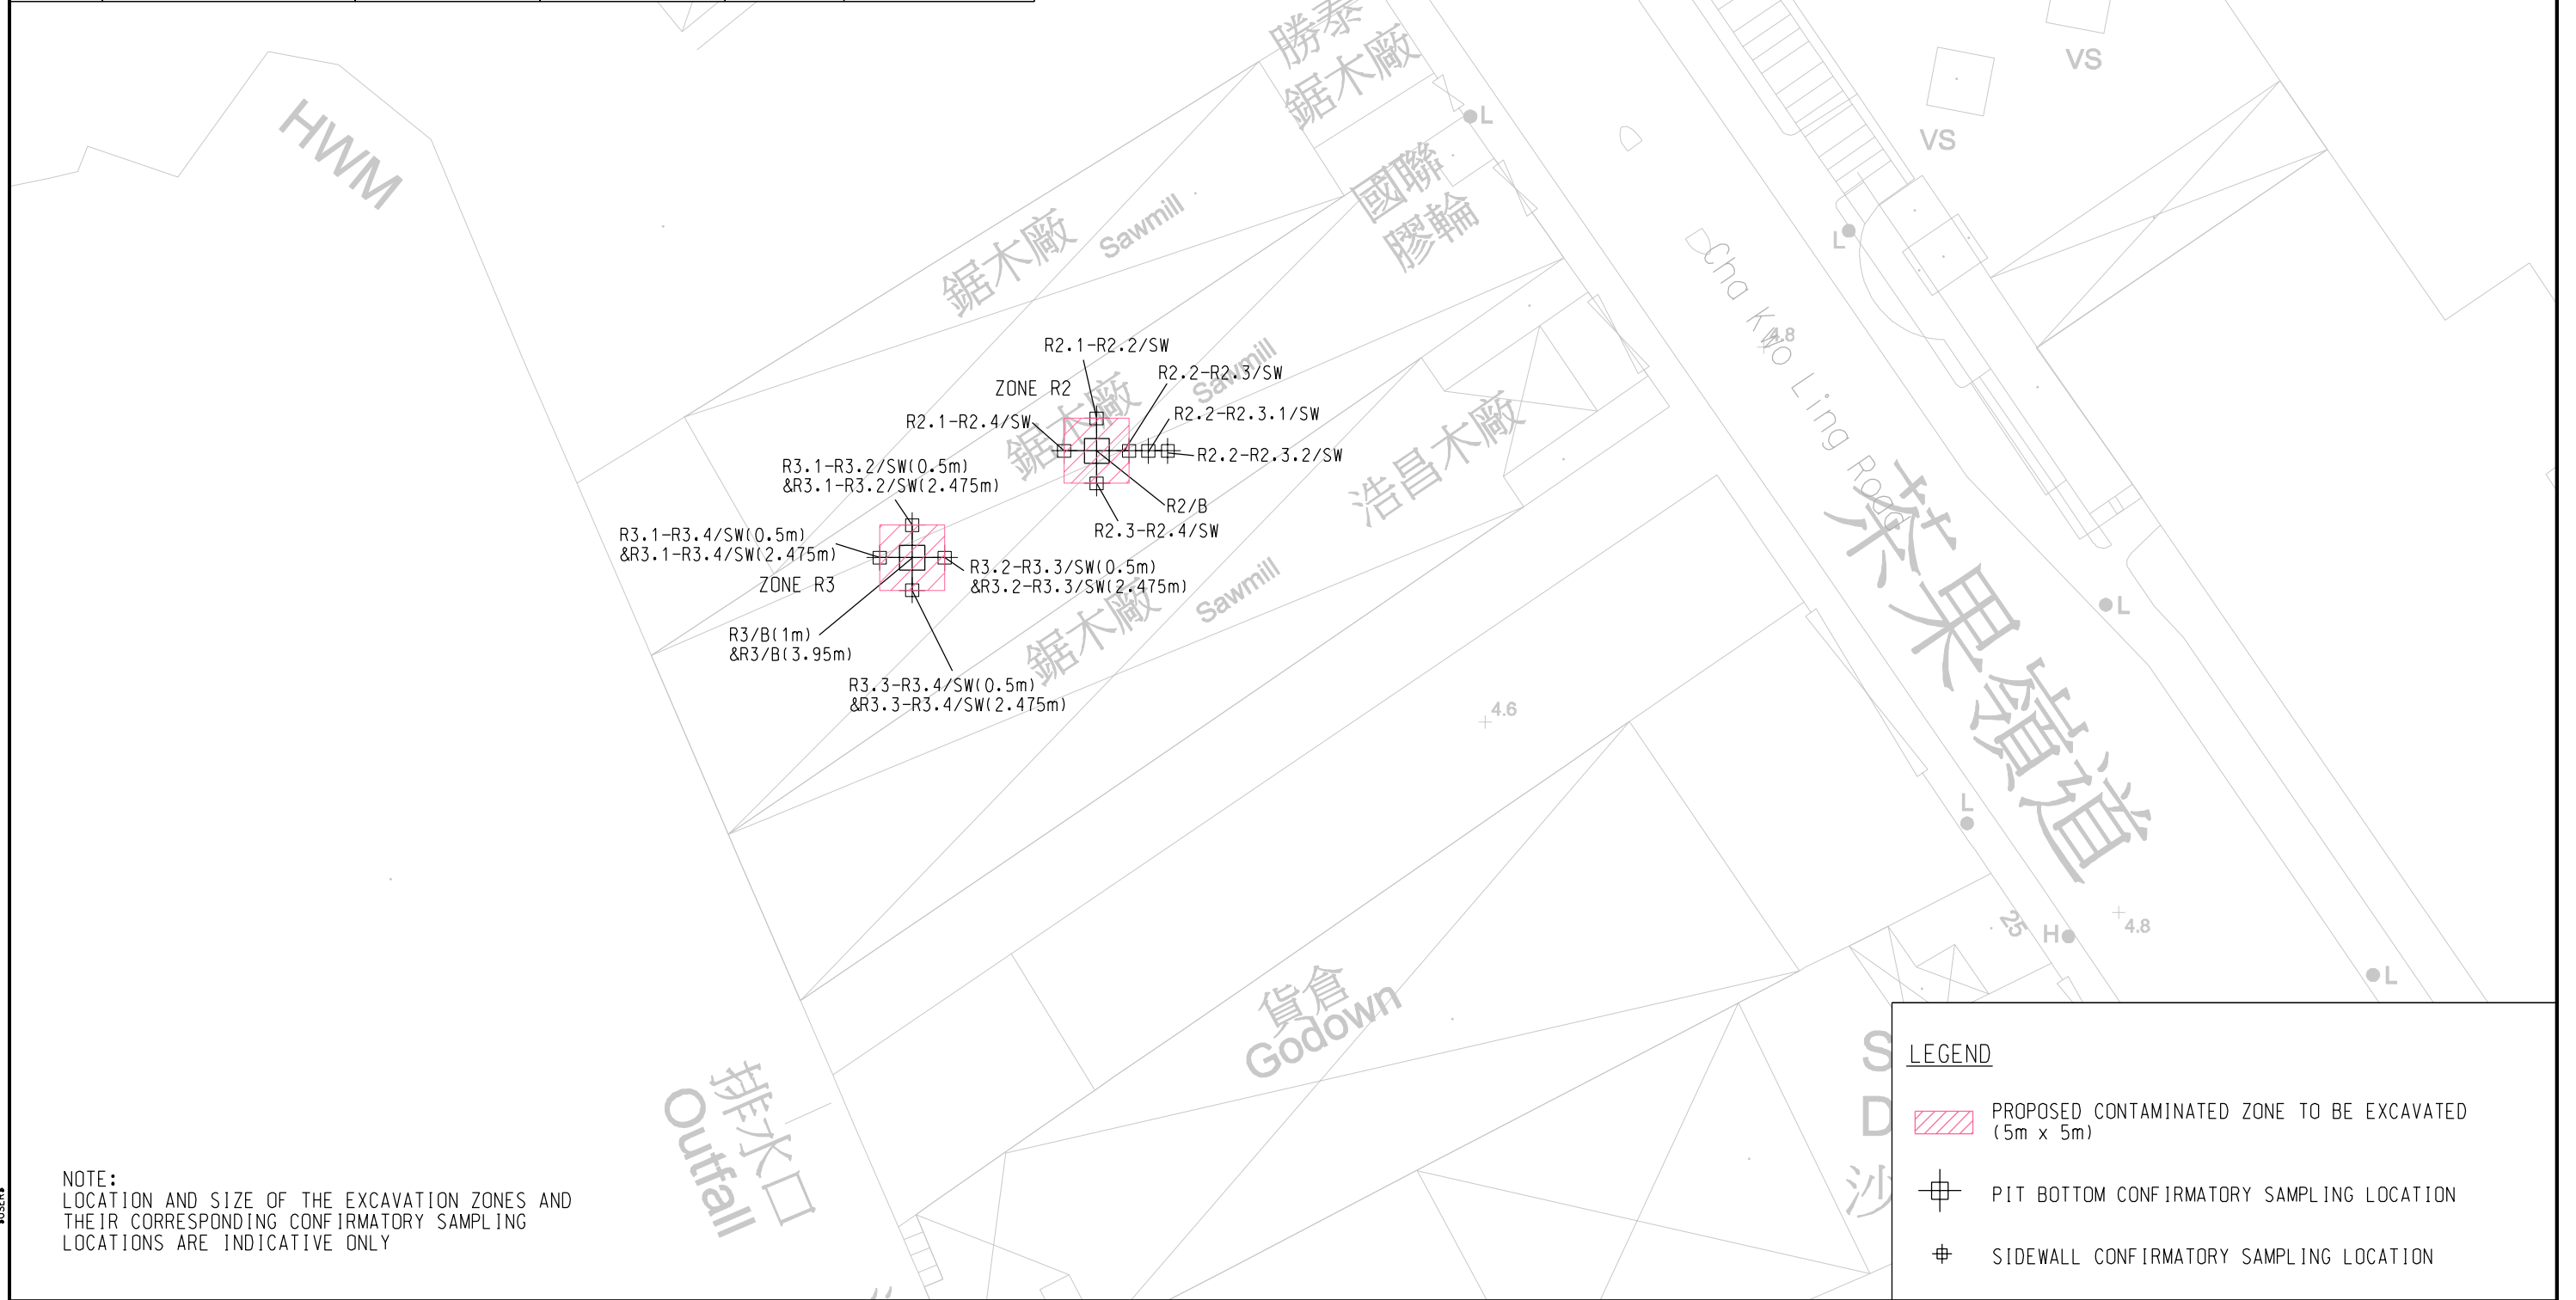

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND THEIR CORRESPONDING CONFIRMATORY SAMPLING LOCATIONS ARE INDICATIVE ONLY

**LEGEND**

- PROPOSED CONTAMINATED ZONE TO BE EXCAVATED (5m x 5m)
- PIT BOTTOM CONFIRMATORY SAMPLING LOCATION
- SIDEWALL CONFIRMATORY SAMPLING LOCATION




YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS

LOCATION OF CONFIRMATORY SAMPLING (ZONES R2 & R3)

|         |            |             |          |
|---------|------------|-------------|----------|
| SCALE   | A3 1 : 500 | DATE        | APR 2014 |
| CHECK   | LLHY       | DRAWN       | KW       |
| JOB No. | 60048208   | DRAWING No. | 7        |
|         |            | REV         | -        |

| ZONE | DEPTH WITH CONTAMINATED SOIL FOUND (m BELOW GROUND SURFACE) | CONTAMINANT IDENTIFIED       | ESTIMATED EXTENT OF CONTAMINATION (m <sup>2</sup> ) | VOLUME (m <sup>3</sup> ) | PROPOSED REMEDIATION METHOD    |
|------|-------------------------------------------------------------|------------------------------|-----------------------------------------------------|--------------------------|--------------------------------|
| R4   | 0-1.0m                                                      | BIS-(2-ETHYLHEXYL)-PHTHALATE | 25                                                  | 25                       | BIOPILING                      |
| R8   | 3.0-4.45m                                                   | LEAD                         | 25                                                  | 36.25                    | SOLIDIFICATION / STABILIZATION |

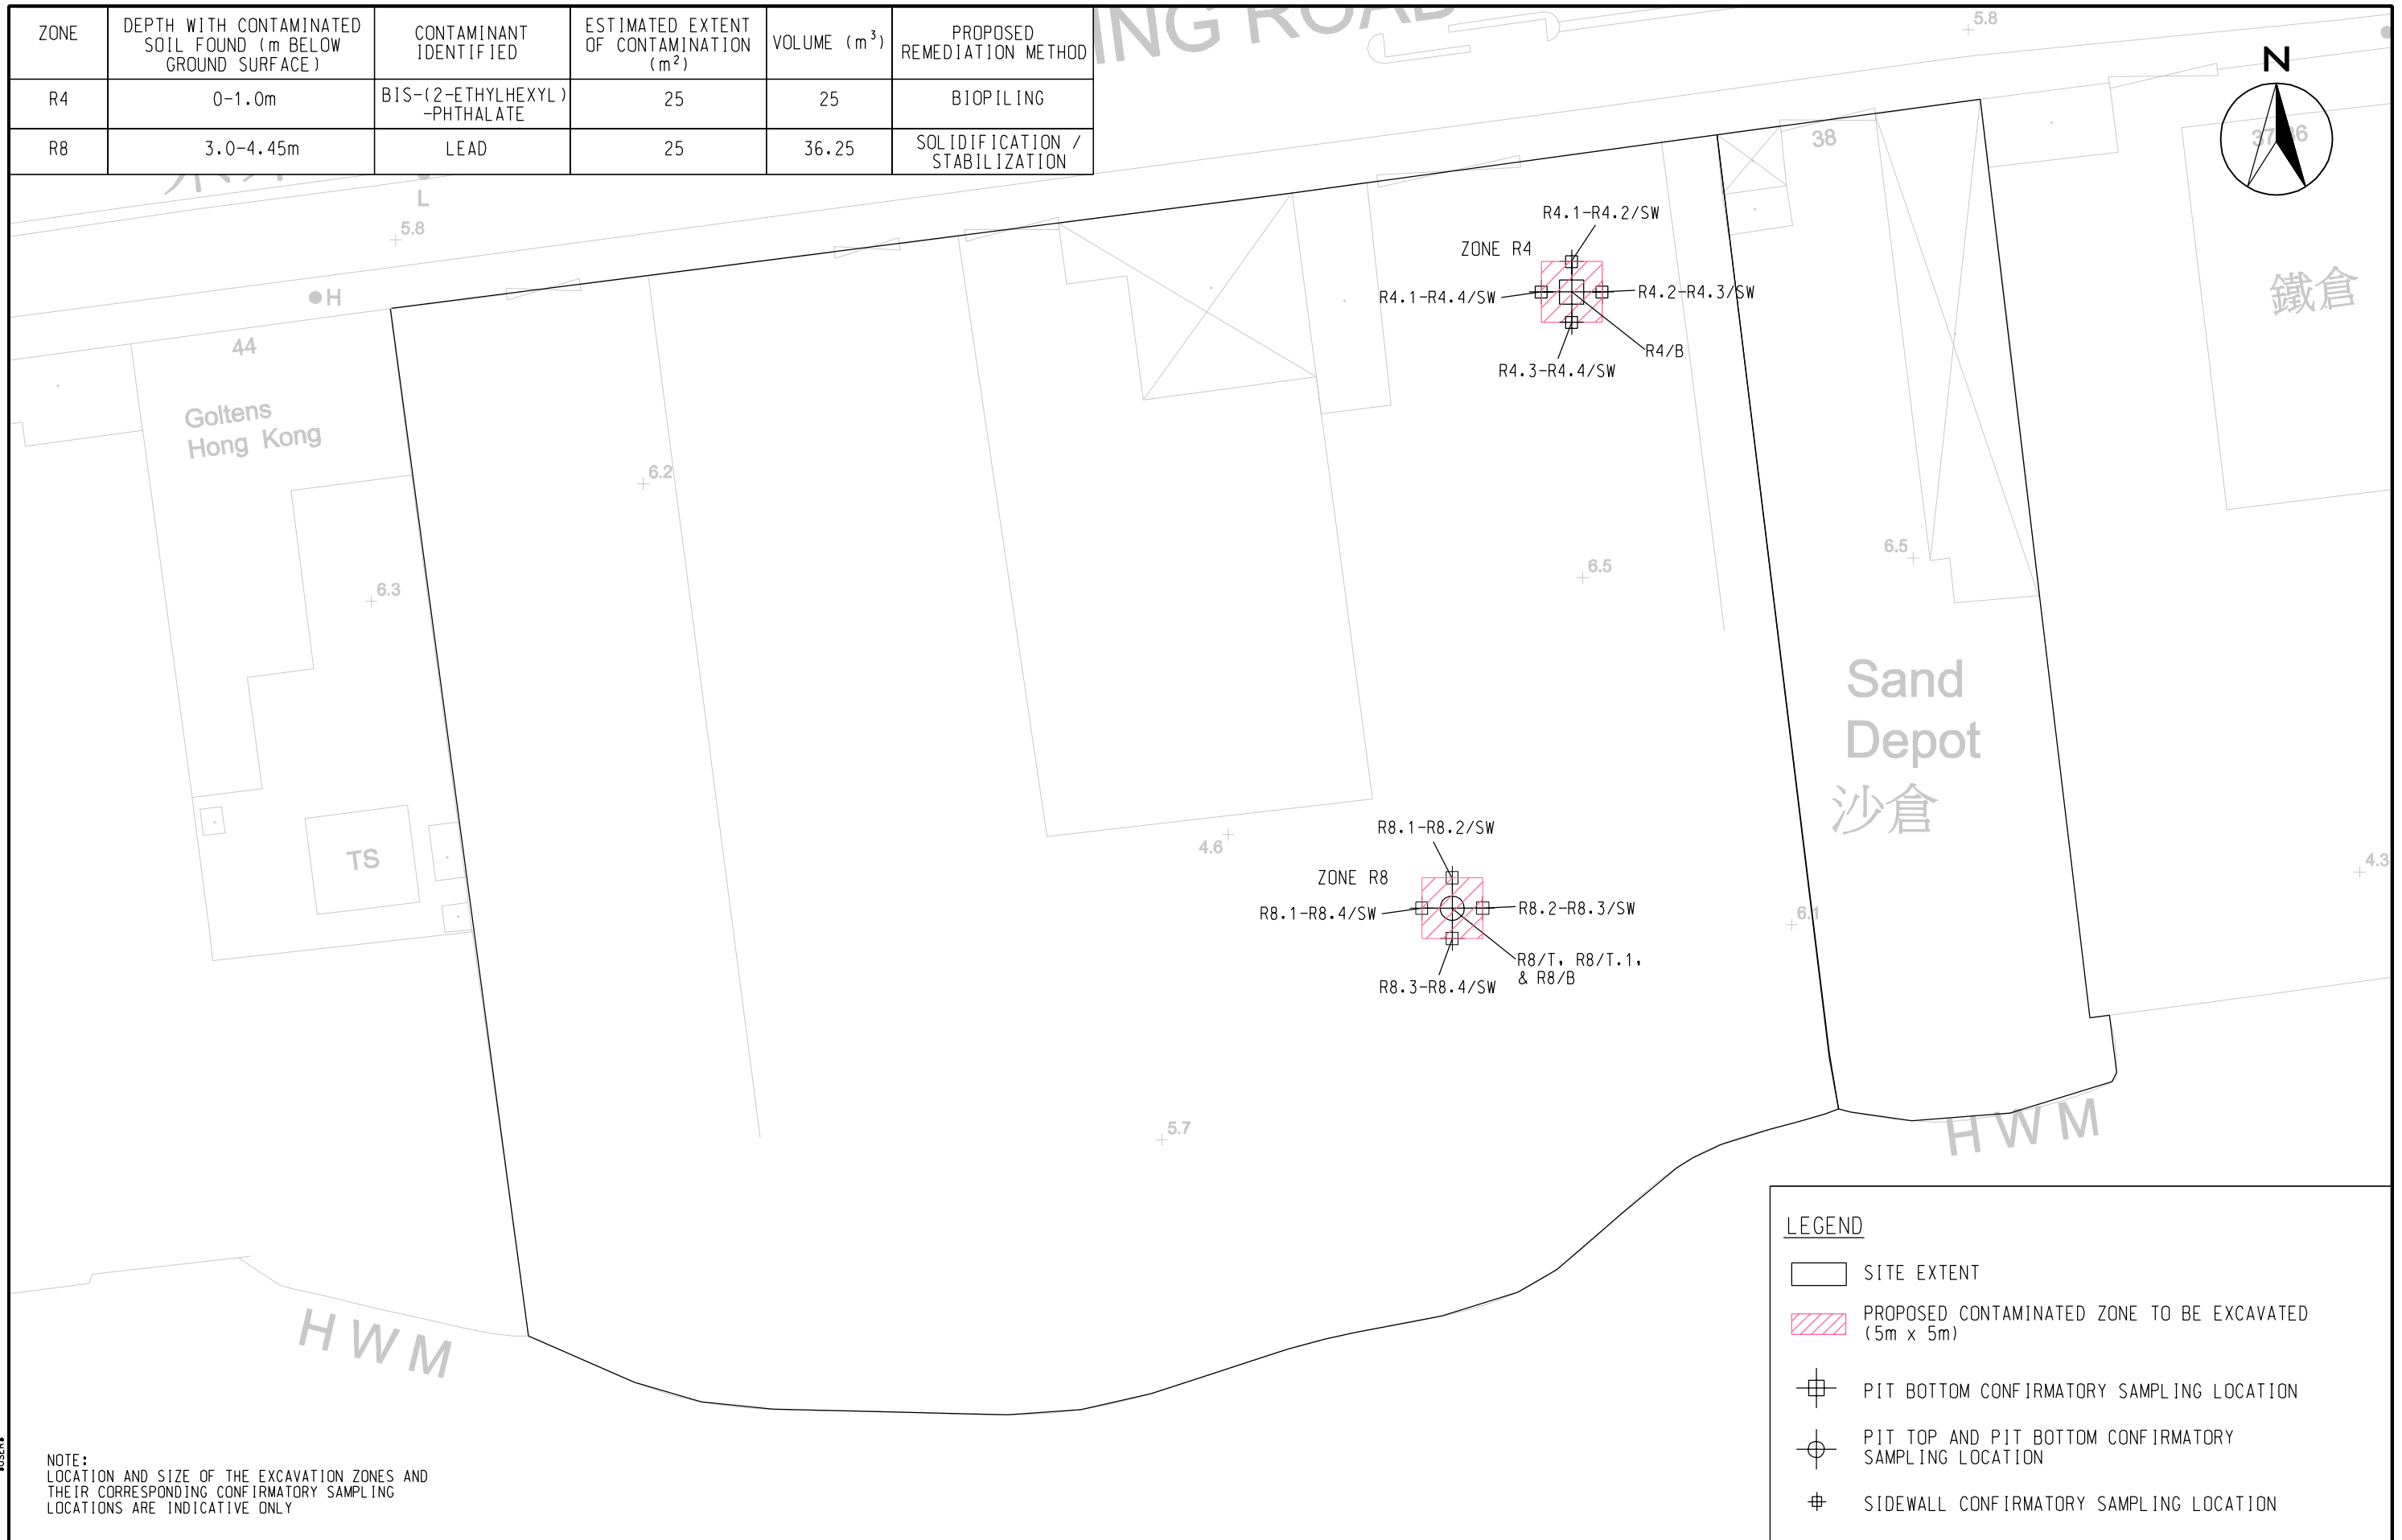

**LEGEND**

- SITE EXTENT
- PROPOSED CONTAMINATED ZONE TO BE EXCAVATED (5m x 5m)
- PIT BOTTOM CONFIRMATORY SAMPLING LOCATION
- PIT TOP AND PIT BOTTOM CONFIRMATORY SAMPLING LOCATION
- SIDEWALL CONFIRMATORY SAMPLING LOCATION

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND THEIR CORRESPONDING CONFIRMATORY SAMPLING LOCATIONS ARE INDICATIVE ONLY



YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS



LOCATION OF CONFIRMATORY SAMPLING (ZONES R4 & R8)

|         |            |             |          |
|---------|------------|-------------|----------|
| SCALE   | A3 1 : 500 | DATE        | APR 2014 |
| CHECK   | LLHY       | DRAWN       | KW       |
| JOB No. | 60048208   | DRAWING No. | 8        |
|         |            | REV         | -        |

Pottling By: DATES



| ZONE | DEPTH WITH CONTAMINATED SOIL FOUND (m BELOW GROUND SURFACE) | CONTAMINANT IDENTIFIED             | ESTIMATED EXTENT OF CONTAMINATION (m <sup>2</sup> ) | VOLUME (m <sup>3</sup> ) | PROPOSED REMEDIATION METHOD               |
|------|-------------------------------------------------------------|------------------------------------|-----------------------------------------------------|--------------------------|-------------------------------------------|
| A2   | 1.0-2.35m                                                   | BIS-(2-ETHYLHEXYL)-PHthalate, LEAD | 31.5                                                | 42.5                     | BIOPILING, SOLIDIFICATION / STABILIZATION |
| A3   | 2.35-4.95m                                                  | LEAD                               | 25                                                  | 65                       | SOLIDIFICATION / STABILIZATION            |
| A4   | 1.0-2.45m                                                   | LEAD                               | 25                                                  | 36.25                    | SOLIDIFICATION / STABILIZATION            |
| A5   | 1.4-2.55m                                                   | LEAD                               | 25                                                  | 28.75                    | SOLIDIFICATION / STABILIZATION            |

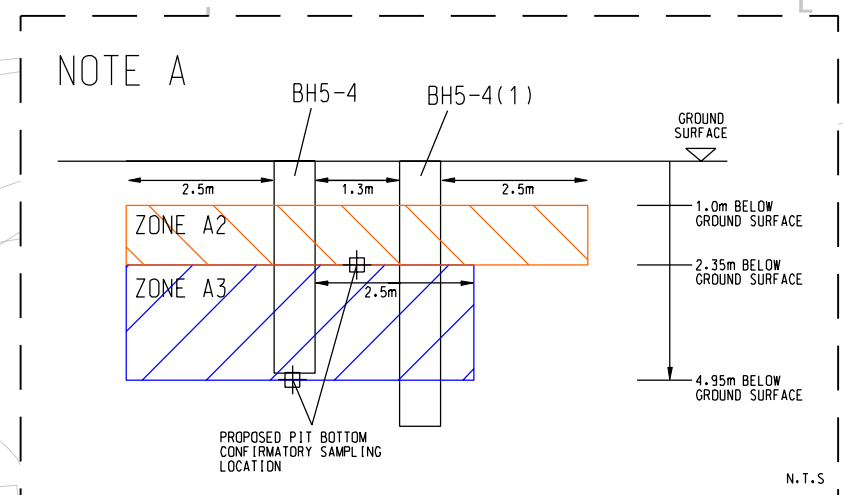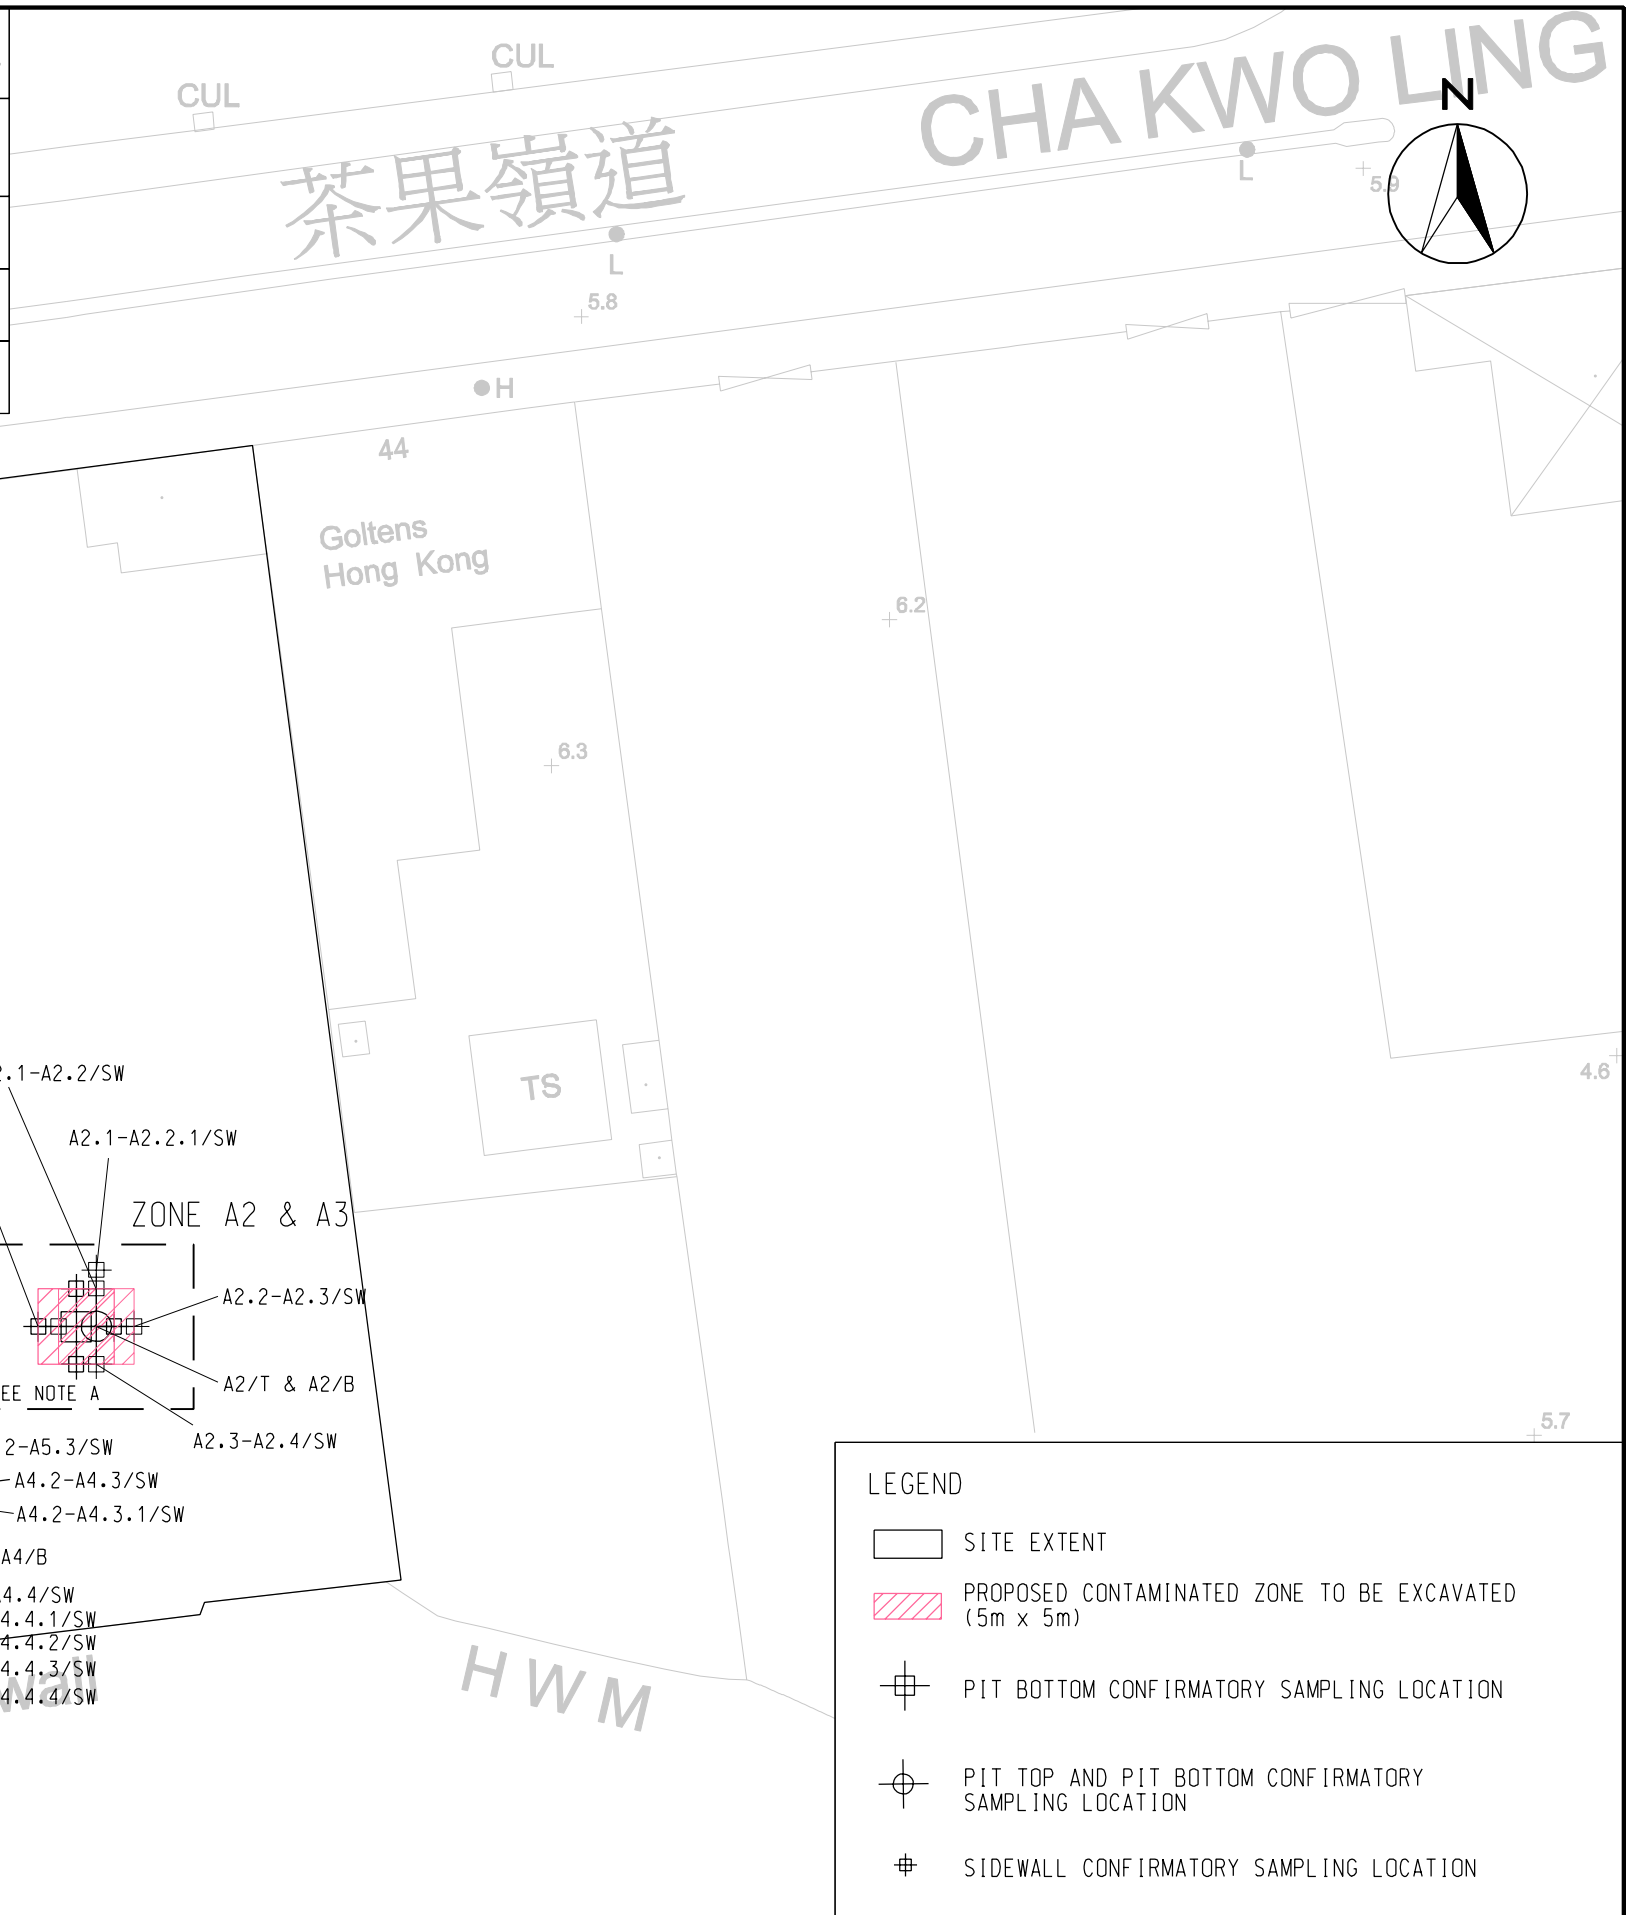

Wing Shan Industrial Building  
 榮山工業大廈

Water Station  
 水站

TS

海堤

HWM

| LEGEND |                                           |  |                                                       |
|--------|-------------------------------------------|--|-------------------------------------------------------|
|        | SITE EXTENT                               |  | PROPOSED CONTAMINATED ZONE TO BE EXCAVATED (5m x 5m)  |
|        | PIT BOTTOM CONFIRMATORY SAMPLING LOCATION |  | PIT TOP AND PIT BOTTOM CONFIRMATORY SAMPLING LOCATION |
|        | SIDEWALL CONFIRMATORY SAMPLING LOCATION   |  |                                                       |





YAU TONG BAY REDEVELOPMENT  
 LAND DECONTAMINATION WORKS

LOCATION OF CONFIRMATORY SAMPLING (ZONES A2, A3, A4 & A5)

|         |            |             |          |
|---------|------------|-------------|----------|
| SCALE   | A3 1 : 500 | DATE        | MAR 2014 |
| CHECK   | LLHY       | DRAWN       | KW       |
| JOB No. | 60048208   | DRAWING No. | 10       |
|         |            | REV         | -        |

| ZONE | DEPTH WITH CONTAMINATED SOIL FOUND (m BELOW GROUND SURFACE) | CONTAMINANT IDENTIFIED | ESTIMATED EXTENT OF CONTAMINATION (m <sup>2</sup> ) | VOLUME (m <sup>3</sup> ) | PROPOSED REMEDIATION METHOD    |
|------|-------------------------------------------------------------|------------------------|-----------------------------------------------------|--------------------------|--------------------------------|
| A1   | 0.0-1.0m                                                    | LEAD                   | 25                                                  | 25                       | SOLIDIFICATION / STABILIZATION |

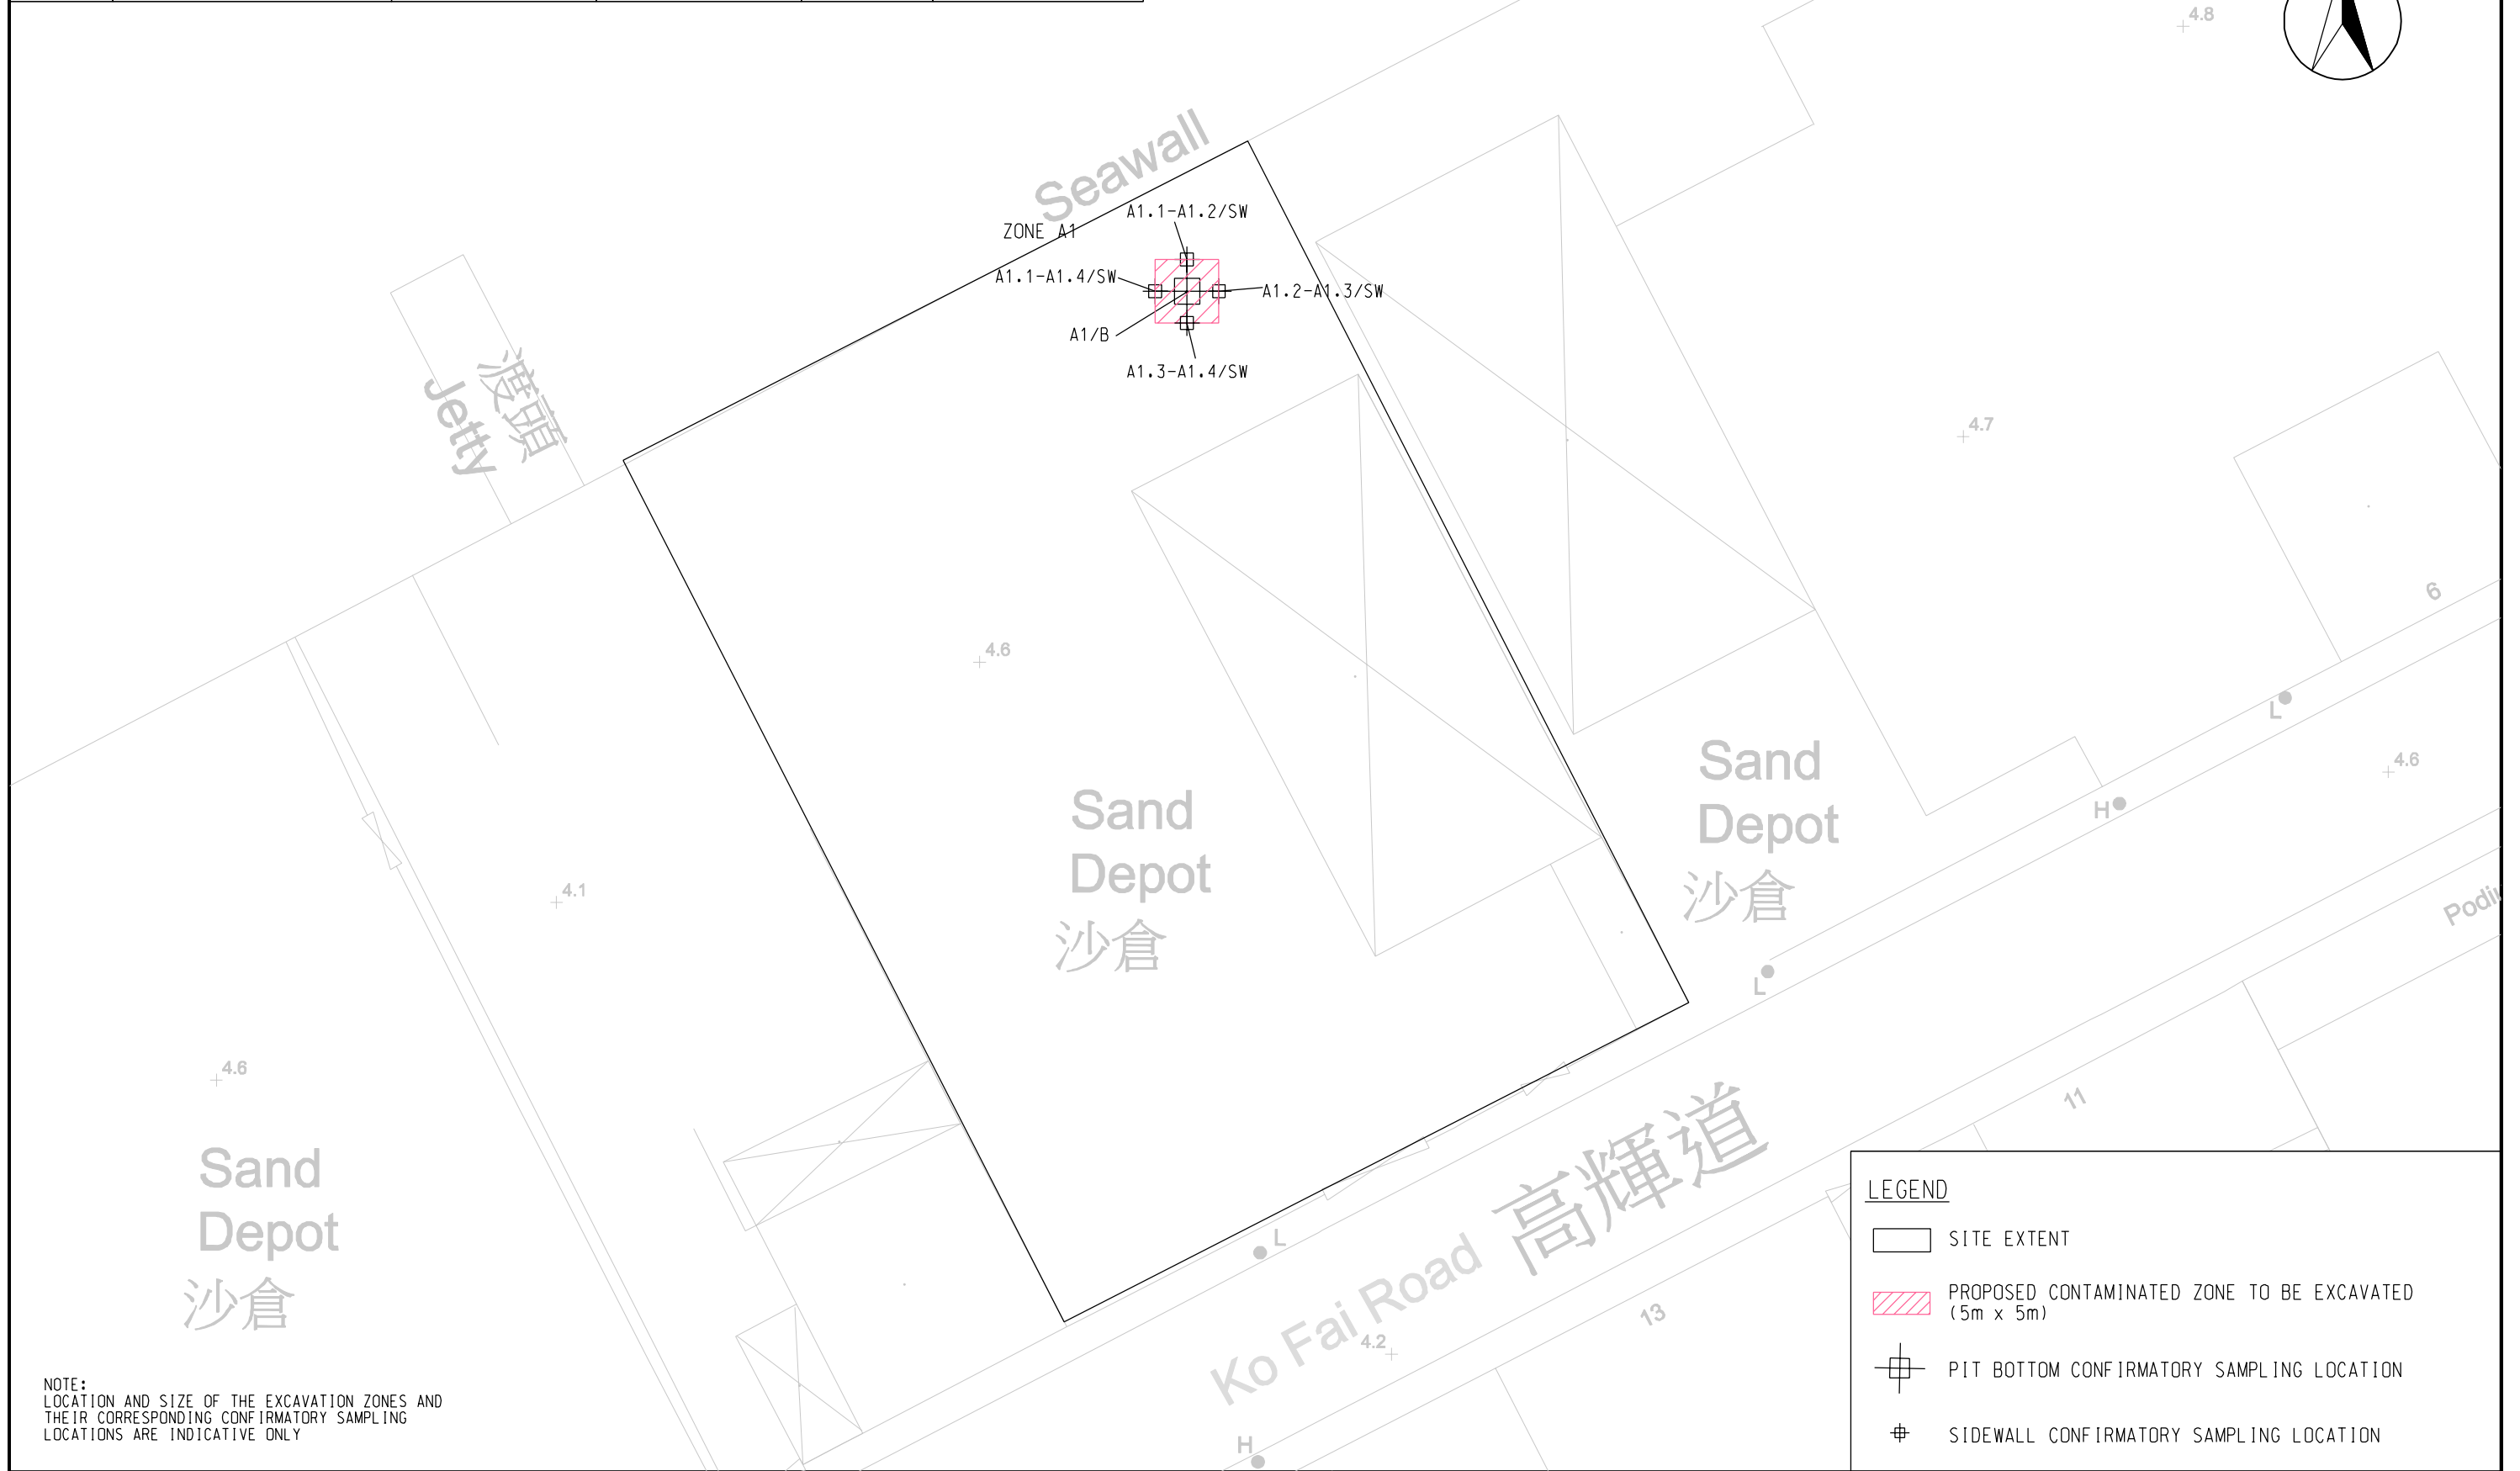

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND THEIR CORRESPONDING CONFIRMATORY SAMPLING LOCATIONS ARE INDICATIVE ONLY

| LEGEND |                                           |  |                                                      |
|--------|-------------------------------------------|--|------------------------------------------------------|
|        | SITE EXTENT                               |  | PROPOSED CONTAMINATED ZONE TO BE EXCAVATED (5m x 5m) |
|        | PIT BOTTOM CONFIRMATORY SAMPLING LOCATION |  | SIDEWALL CONFIRMATORY SAMPLING LOCATION              |




YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS

LOCATION OF CONFIRMATORY SAMPLING (ZONE A1)

|         |            |             |          |
|---------|------------|-------------|----------|
| SCALE   | A3 1 : 500 | DATE        | MAR 2014 |
| CHECK   | LLHY       | DRAWN       | KW       |
| JOB No. | 60048208   | DRAWING No. | 9        |
|         |            | REV         | -        |

| ZONE | DEPTH WITH CONTAMINATED SOIL FOUND (m BELOW GROUND SURFACE) | CONTAMINANT IDENTIFIED | ESTIMATED EXTENT OF CONTAMINATION (m <sup>2</sup> ) | VOLUME (m <sup>3</sup> ) | PROPOSED REMEDIATION METHOD               |
|------|-------------------------------------------------------------|------------------------|-----------------------------------------------------|--------------------------|-------------------------------------------|
| T32C | 1.5-3.5                                                     | LEAD                   | 78.5                                                | 157                      | SOLIDIFICATION / STABILIZATION            |
| T32D | 0.5-1.5                                                     | PCB                    | 78.5                                                | 78.5                     | LANDFILL DISPOSAL                         |
| T32E | 0-1.5                                                       | TPH                    | 654.2                                               | 750.5                    | BIOPILING, SOLIDIFICATION / STABILIZATION |
| T32E | 0-3                                                         | PCB                    | 153.9                                               | 461.6                    | LANDFILL DISPOSAL                         |
| T36A | 0-1.5                                                       | LEAD                   | 153.9                                               | 117.75                   | SOLIDIFICATION / STABILIZATION            |

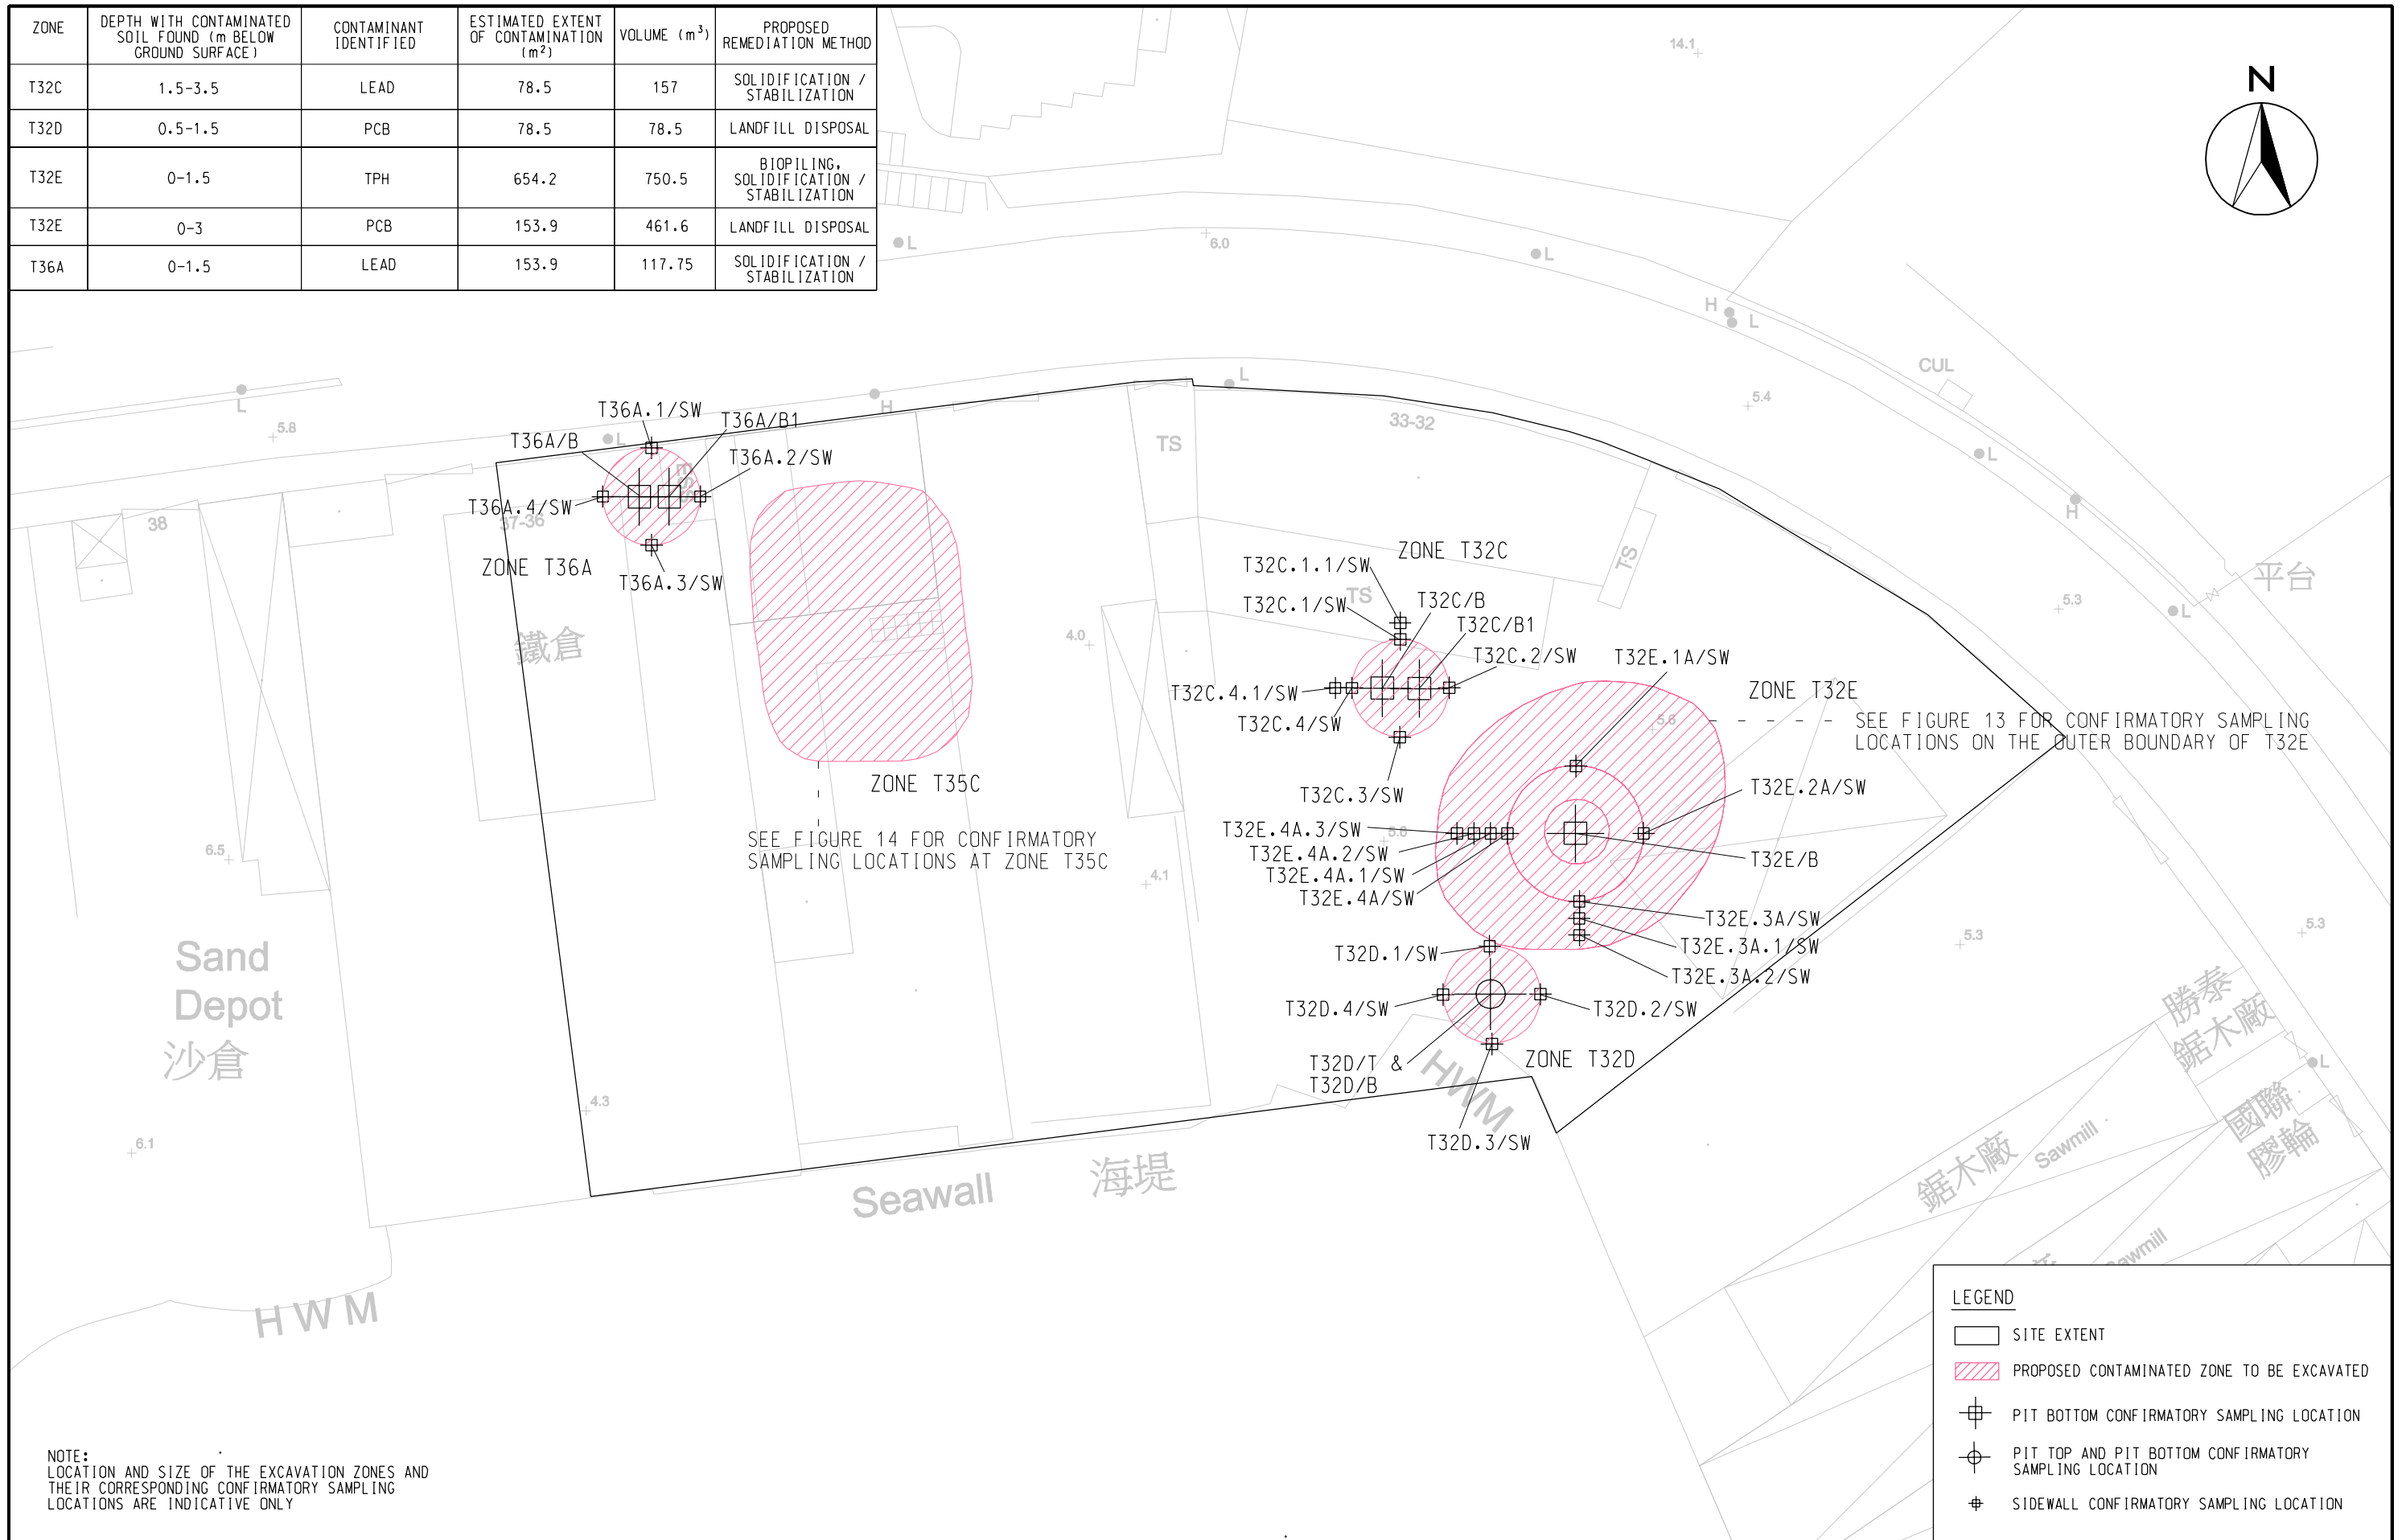

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND THEIR CORRESPONDING CONFIRMATORY SAMPLING LOCATIONS ARE INDICATIVE ONLY

| LEGEND |                                                       |
|--------|-------------------------------------------------------|
|        | SITE EXTENT                                           |
|        | PROPOSED CONTAMINATED ZONE TO BE EXCAVATED            |
|        | PIT BOTTOM CONFIRMATORY SAMPLING LOCATION             |
|        | PIT TOP AND PIT BOTTOM CONFIRMATORY SAMPLING LOCATION |
|        | SIDEWALL CONFIRMATORY SAMPLING LOCATION               |




YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS

LOCATION OF CONFIRMATORY SAMPLING (ZONES T32C, T32D, T32E, T35C AND T36A)




|             |            |            |          |
|-------------|------------|------------|----------|
| SCALE       | A3 1 : 600 | DATE       | MAR 2014 |
| CHECK       | LLHY       | DRAWN      | KW       |
| PROJECT NO. | 60048208   | FIGURE NO. | 11       |
|             |            | REV        | -        |

| ZONE  | DEPTH WITH CONTAMINATED SOIL FOUND (m BELOW GROUND SURFACE) | CONTAMINANT IDENTIFIED | ESTIMATED EXTENT OF CONTAMINATION (m <sup>2</sup> ) | VOLUME (m <sup>3</sup> ) | PROPOSED REMEDIATION METHOD    |
|-------|-------------------------------------------------------------|------------------------|-----------------------------------------------------|--------------------------|--------------------------------|
| T19A  | 0.5-2.0                                                     | LEAD                   | 78.5                                                | 117.75                   | SOLIDIFICATION / STABILIZATION |
| T22BA | 0.0-1.5                                                     | LEAD                   | 78.5                                                | 117.75                   | SOLIDIFICATION / STABILIZATION |
| T22BB | 1.5-3.0                                                     | LEAD & COPPER          | 153.9                                               | 230.8                    | SOLIDIFICATION / STABILIZATION |

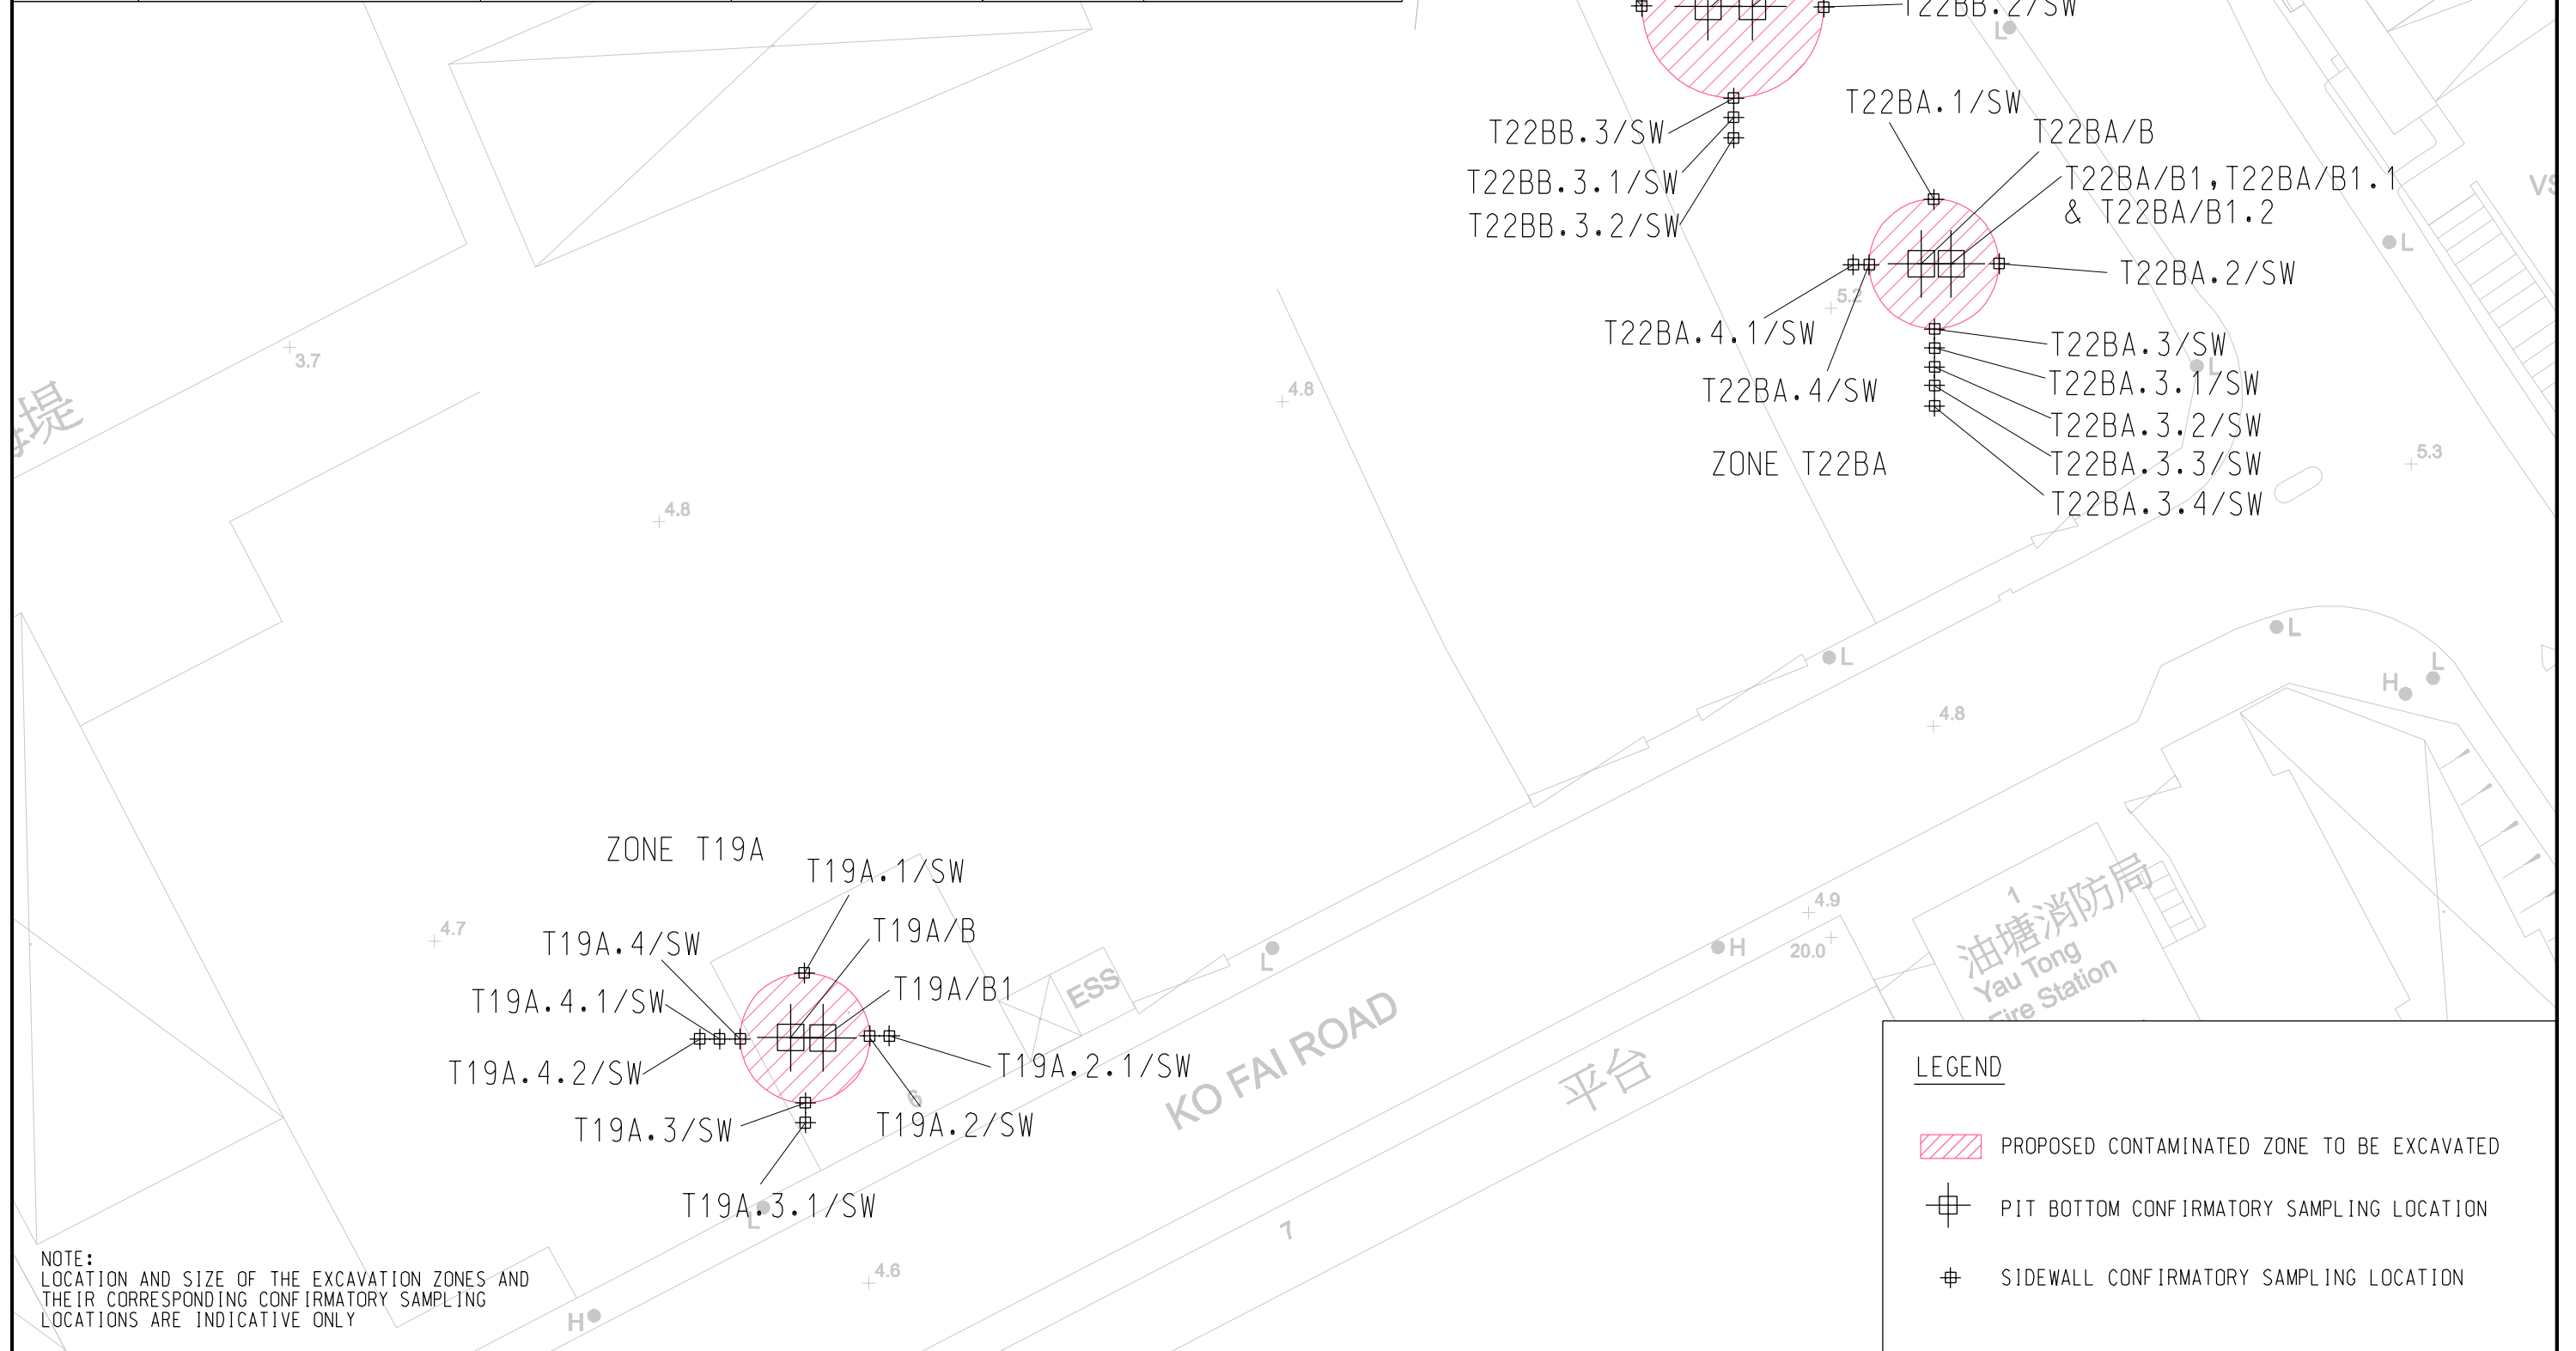

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND THEIR CORRESPONDING CONFIRMATORY SAMPLING LOCATIONS ARE INDICATIVE ONLY

**LEGEND**


-  PROPOSED CONTAMINATED ZONE TO BE EXCAVATED
-  PIT BOTTOM CONFIRMATORY SAMPLING LOCATION
-  SIDEWALL CONFIRMATORY SAMPLING LOCATION



YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS

LOCATION OF CONFIRMATORY SAMPLING (ZONES T19A, T22BA, T22BB)

|             |            |            |          |
|-------------|------------|------------|----------|
| SCALE       | A3 1 : 500 | DATE       | MAR 2014 |
| CHECK       | LLHY       | DRAWN      | KW       |
| PROJECT NO. | 60048208   | FIGURE NO. | 12       |
|             |            | REV        | -        |

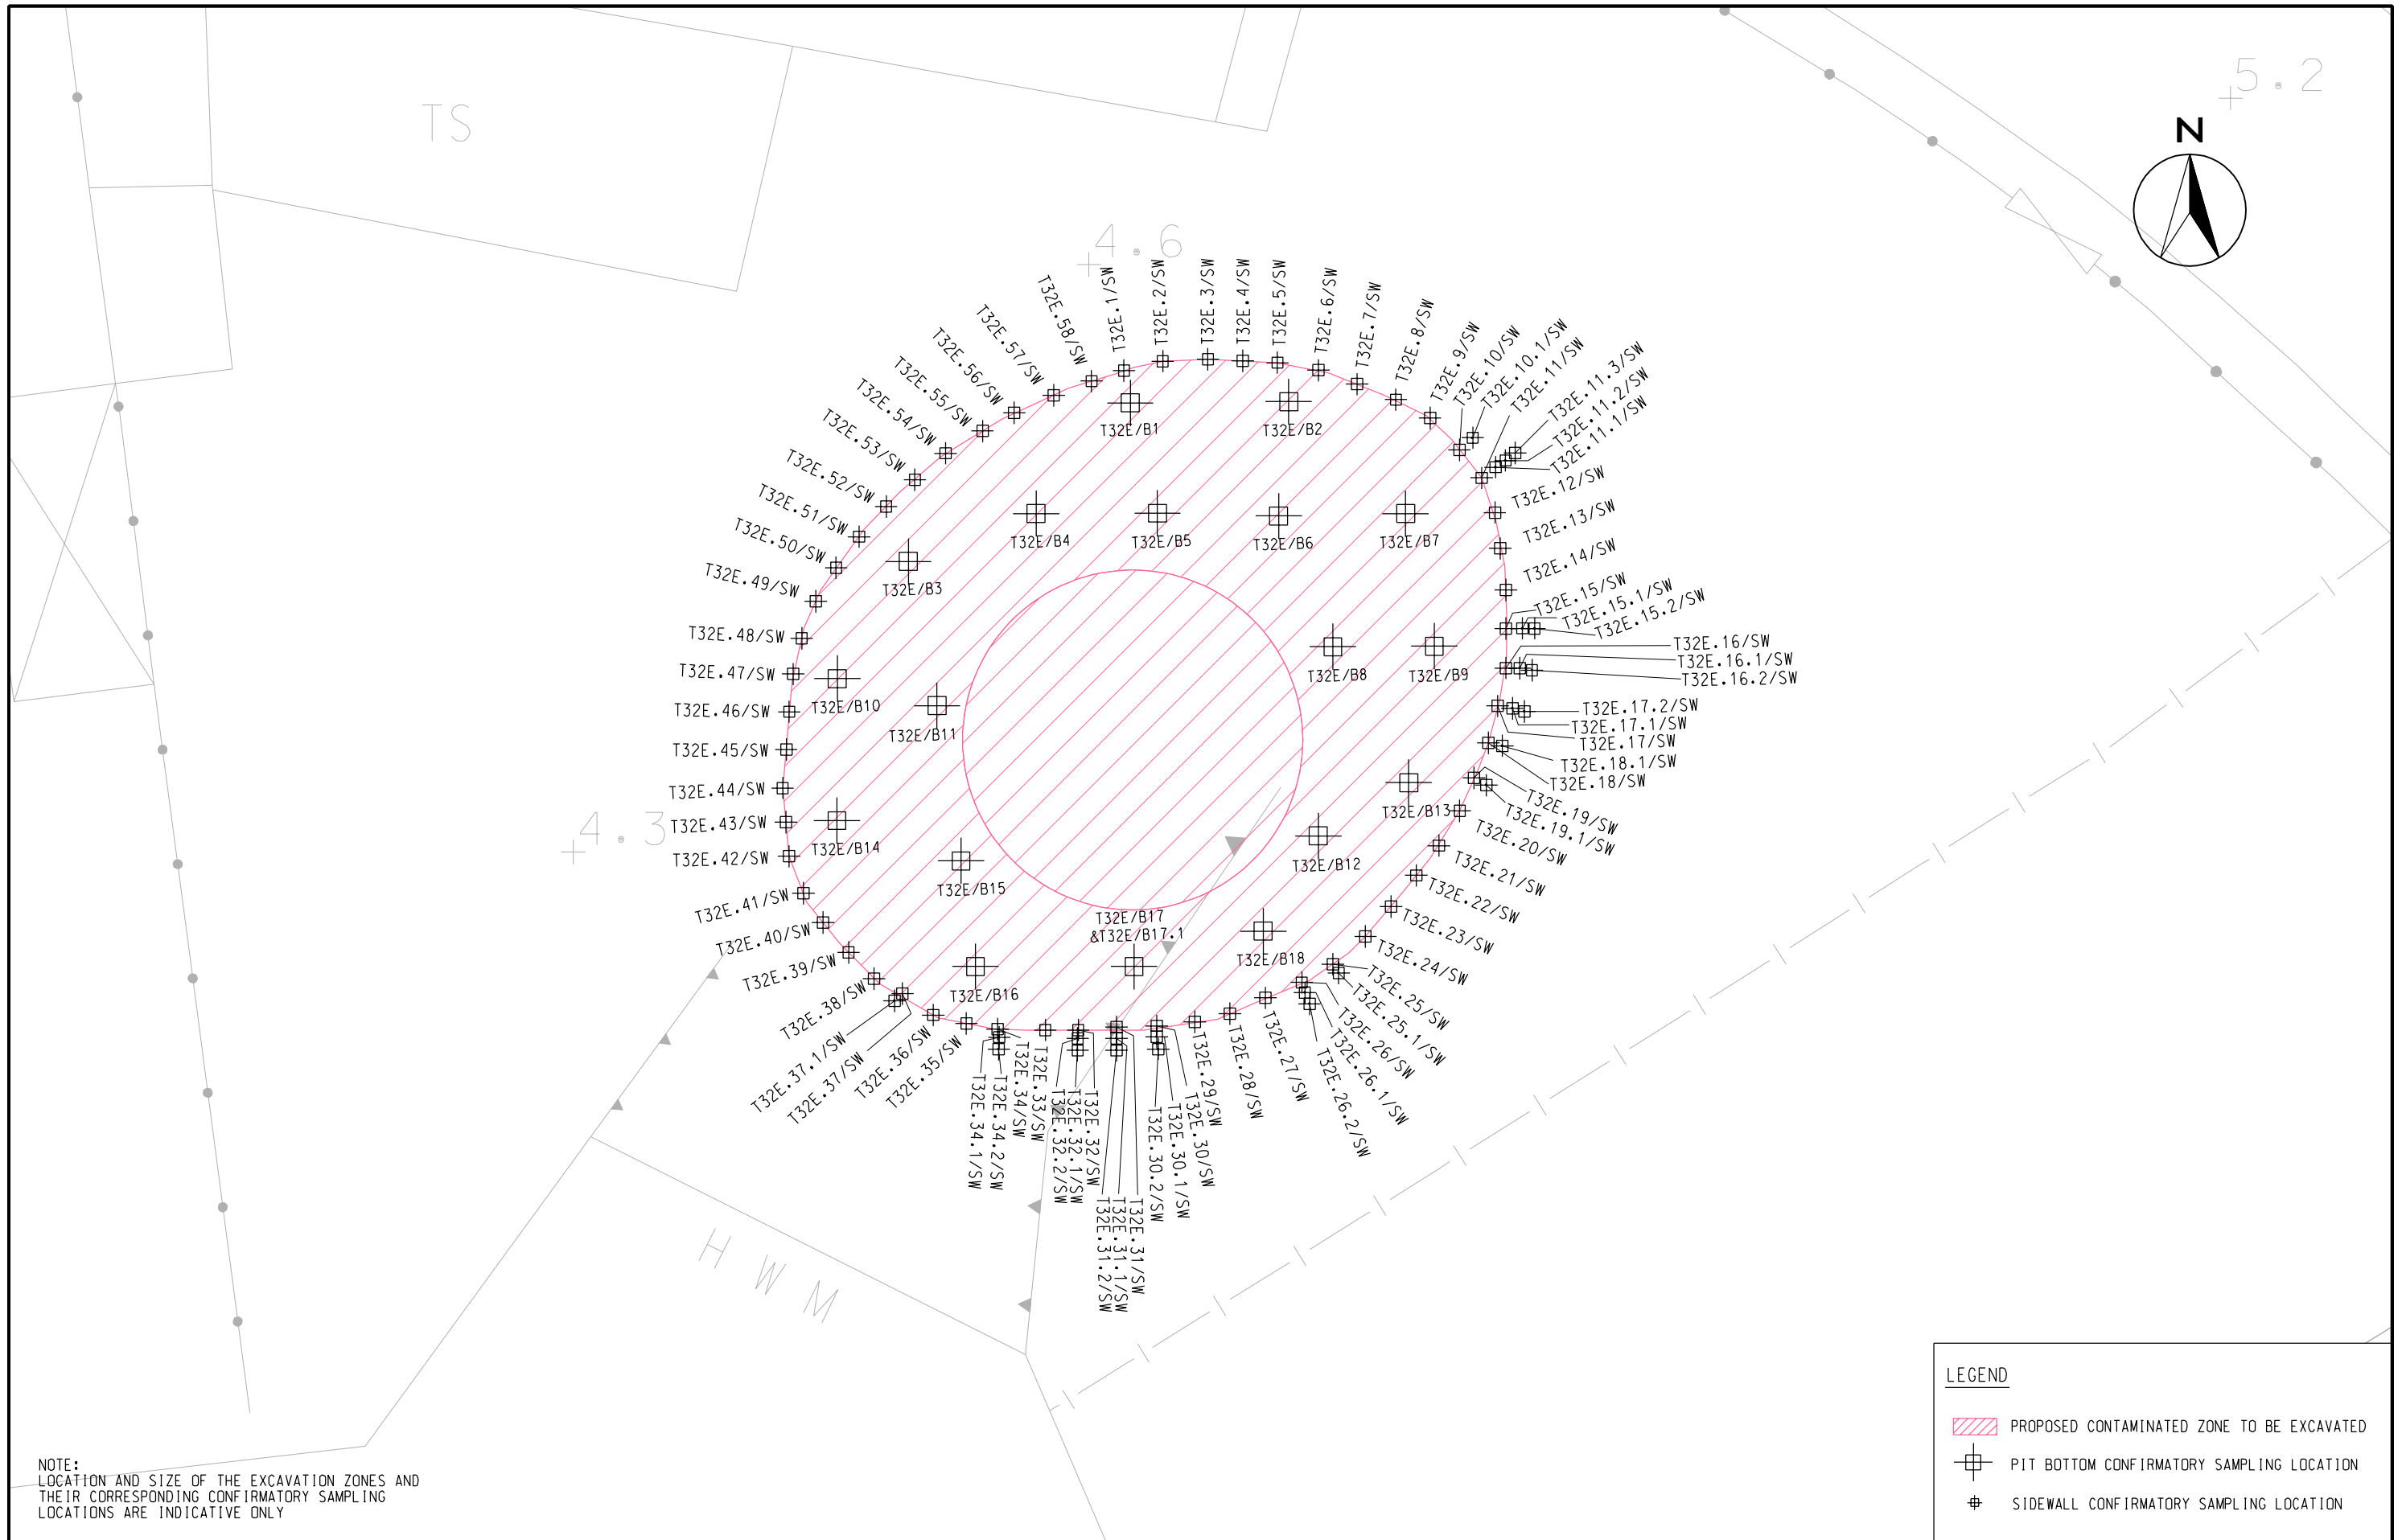

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND  
THEIR CORRESPONDING CONFIRMATORY SAMPLING  
LOCATIONS ARE INDICATIVE ONLY

| LEGEND |                                            |  |
|--------|--------------------------------------------|--|
|        | PROPOSED CONTAMINATED ZONE TO BE EXCAVATED |  |
|        | PIT BOTTOM CONFIRMATORY SAMPLING LOCATION  |  |
|        | SIDEWALL CONFIRMATORY SAMPLING LOCATION    |  |



YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS

LOCATION OF CONFIRMATORY SAMPLING (ZONE T32E)



|             |          |            |          |
|-------------|----------|------------|----------|
| SCALE       | A3 1:250 | DATE       | APR 2014 |
| CHECK       | LLHY     | DRAWN      | KW       |
| PROJECT NO. | 60048208 | FIGURE NO. | 13       |
|             |          | REV        | -        |



37-36

鐵倉




ESS

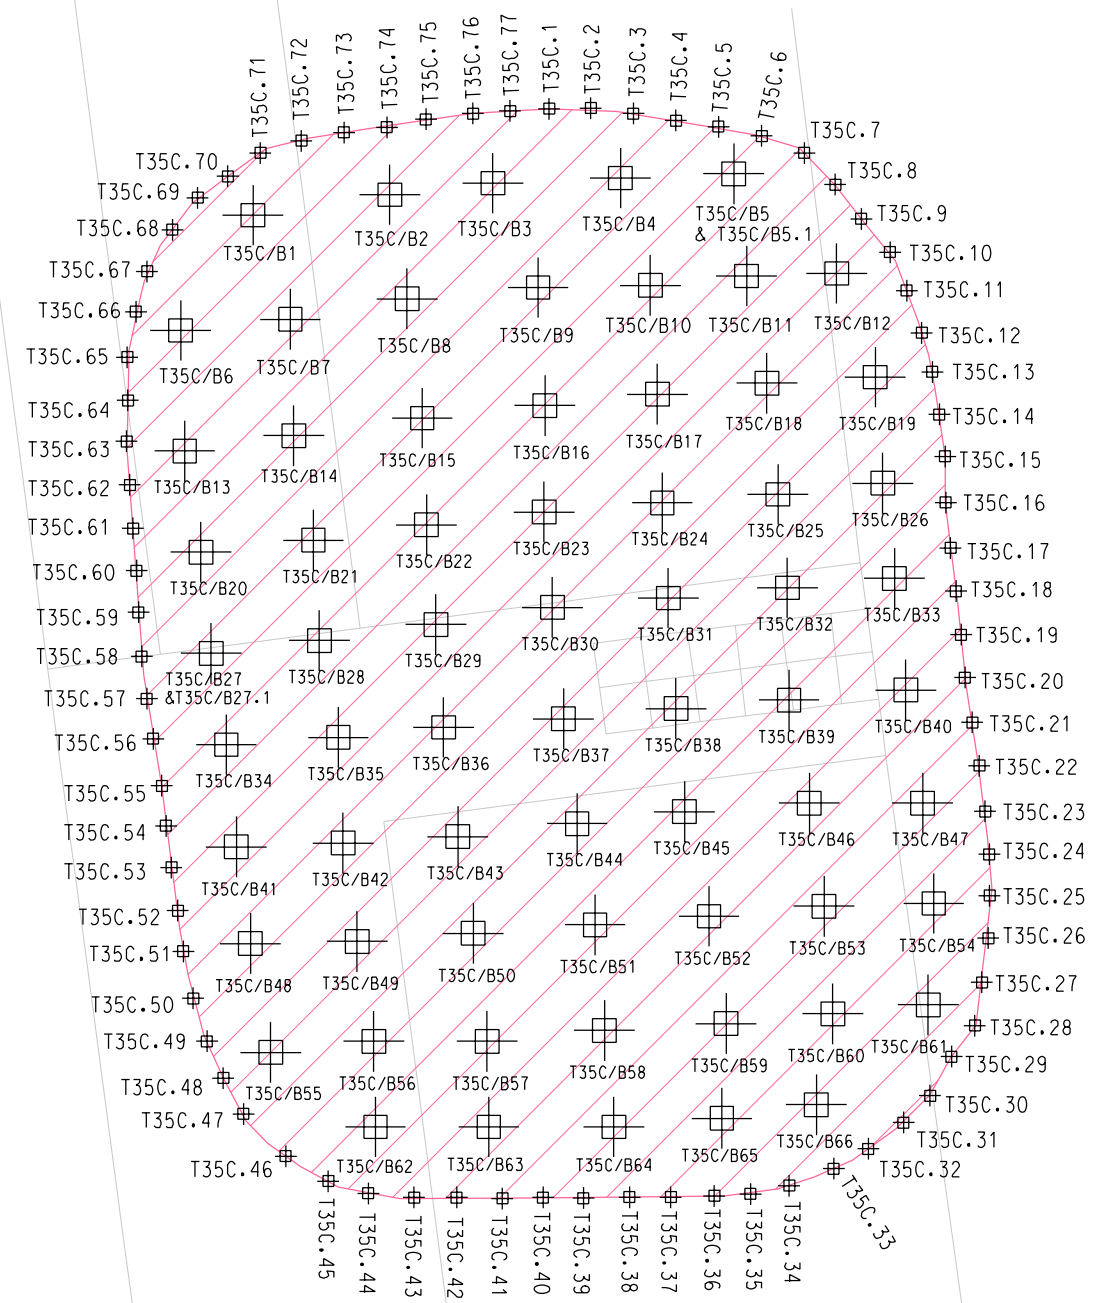

4.0 +

NOTE:  
LOCATION AND SIZE OF THE EXCAVATION ZONES AND  
THEIR CORRESPONDING CONFIRMATORY SAMPLING  
LOCATIONS ARE INDICATIVE ONLY

LEGEND

-  PROPOSED CONTAMINATED ZONE TO BE EXCAVATED
-  PIT BOTTOM CONFIRMATORY SAMPLING LOCATION
-  SIDEWALL CONFIRMATORY SAMPLING LOCATION



YAU TONG BAY REDEVELOPMENT  
LAND DECONTAMINATION WORKS  
LOCATION OF CONFIRMATORY SAMPLING (T35C)

|             |            |            |          |
|-------------|------------|------------|----------|
| SCALE       | A3 1 : 200 | DATE       | APR 2014 |
| CHECK       | LLHY       | DRAWN      | KW       |
| PROJECT NO. | 60048208   | FIGURE NO. | 14       |
|             |            | REV        | -        |


---

---

**APPENDIX A  
PROJECT ORGANIZATION STRUCTURE**

---

---

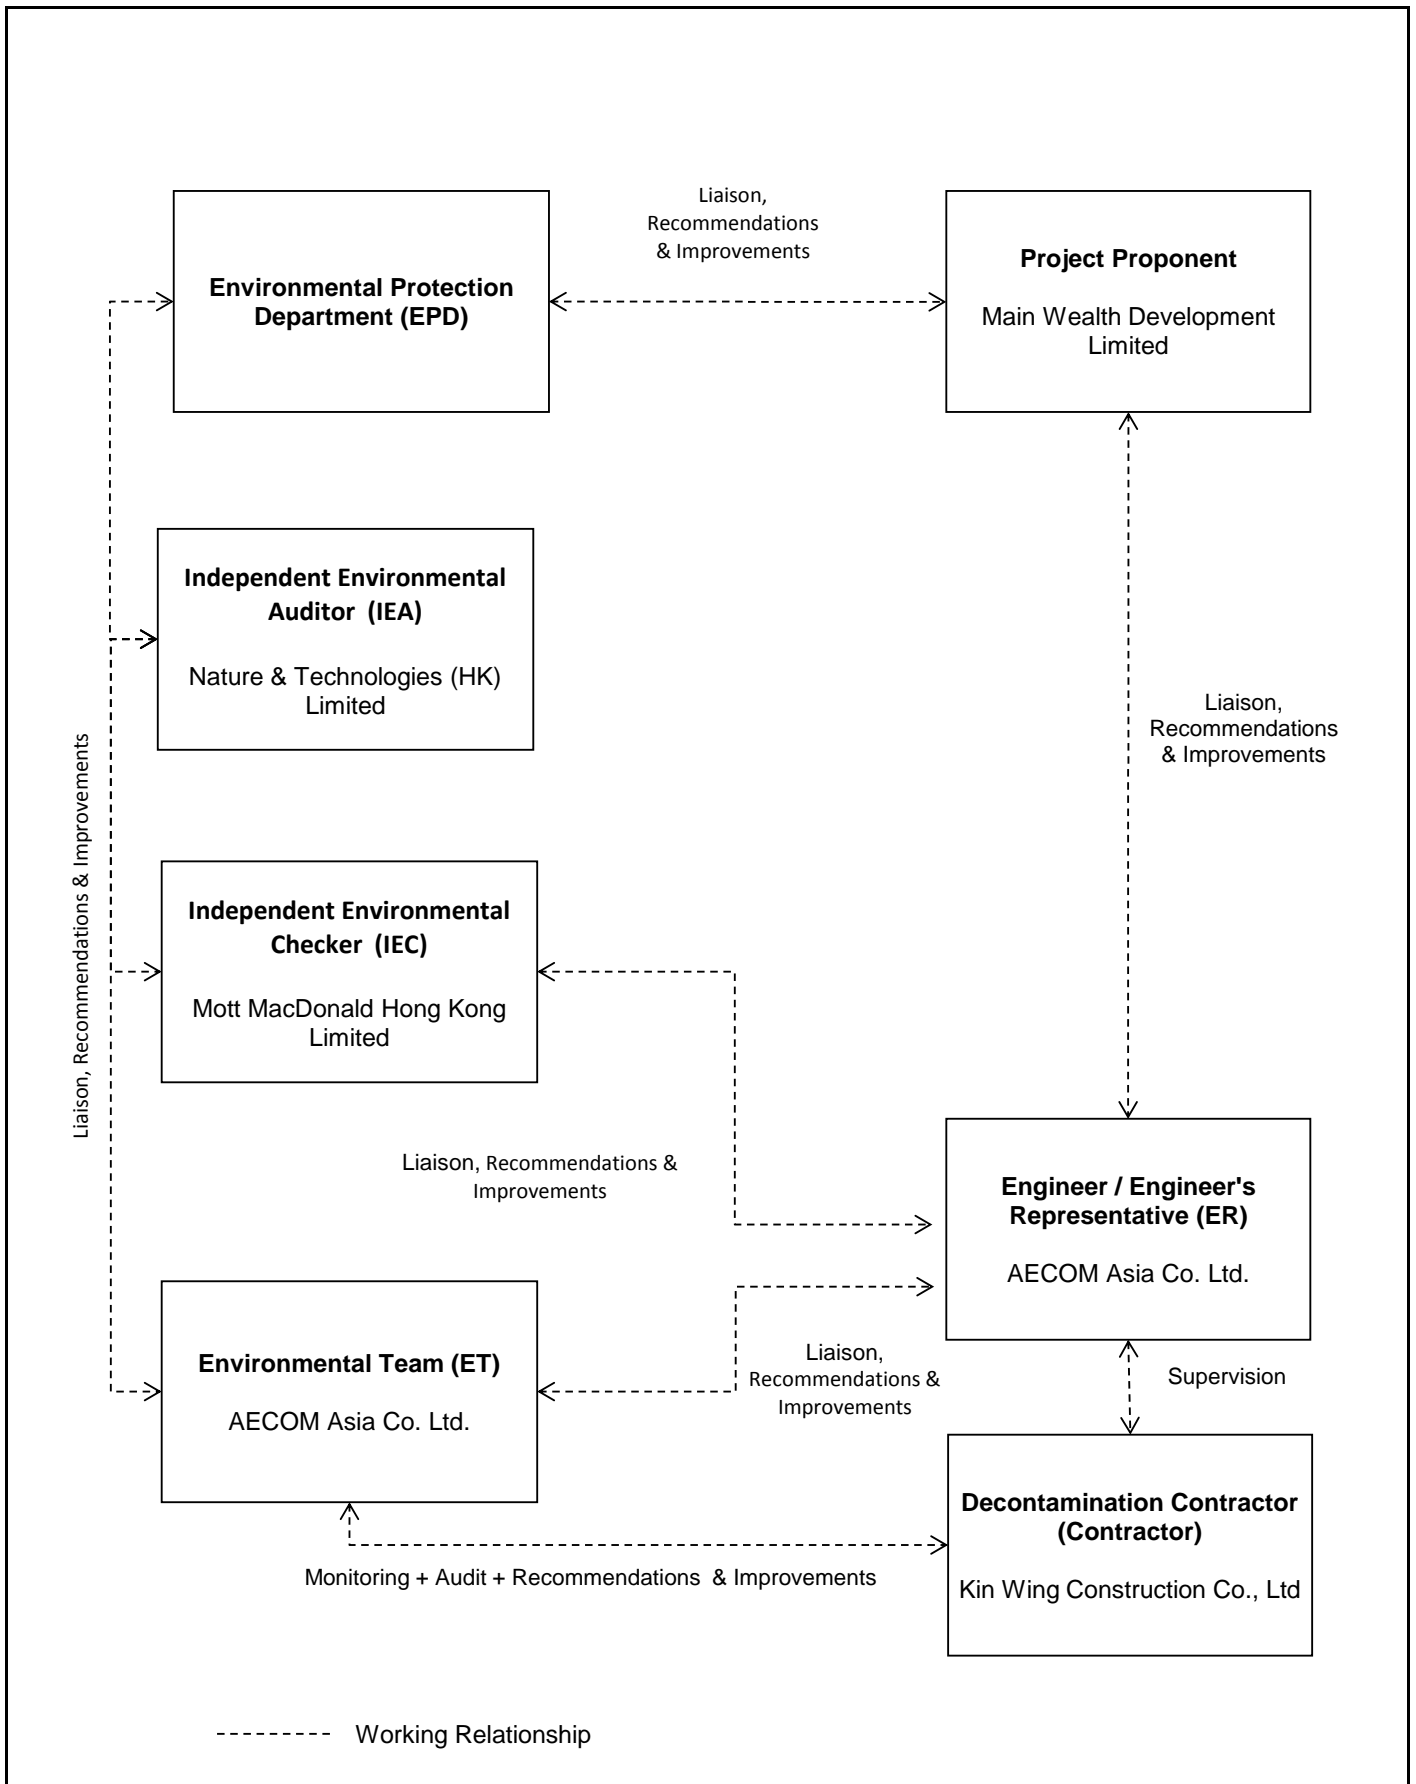

|              |                                                         |         |          |          |        |
|--------------|---------------------------------------------------------|---------|----------|----------|--------|
| <b>AECOM</b> | <b>Yau Tong Bay - Decommissioning of Shipyard Sites</b> | SCALE   | N.T.S.   | DATE     | Dec-13 |
|              |                                                         | CHECK   | ENFL     | DRAWN    | JCYK   |
|              | Project Organization Structure                          | JOB NO. | 60048283 | APPENDIX | A      |



---

---

**APPENDIX B  
CONSTRUCTION PROGRAMME**



---

---

# Yau Tong Bay Redevelopment Land Decontamination Works

## Construction Programme (Rev. 2)

| I.D No. | Start     | Finish    | 2013 |     |     |     | 2014 |     |     |     |     |     |     |     |      |     |     |     | 2015 |
|---------|-----------|-----------|------|-----|-----|-----|------|-----|-----|-----|-----|-----|-----|-----|------|-----|-----|-----|------|
|         |           |           | Sept | Oct | Nov | Dec | Jan  | Feb | Mar | Apr | May | Jun | Jul | Aug | Sept | Oct | Nov | Dec | Jan  |
| 10      | 13-Sep-13 | 27-Nov-13 | █    | █   | █   |     |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 20      | 30-Sep-13 | 16-Dec-13 |      | █   | █   | █   | █    |     |     |     |     |     |     |     |      |     |     |     |      |
| 30      | 13-Sep-13 | 23-Oct-13 | █    | █   |     |     |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 40      | 24-Oct-13 | 23-Jan-14 |      |     | █   | █   | █    | █   |     |     |     |     |     |     |      |     |     |     |      |
| 42      | 28-Oct-13 | 5-Jan-15  |      |     | █   | █   | █    | █   | █   | █   | █   | █   | █   | █   | █    | █   | █   | █   | █    |
| 45      | 11-Nov-13 | 16-Dec-13 |      |     | █   | █   | █    |     |     |     |     |     |     |     |      |     |     |     |      |
| 50      | 28-Oct-13 | 23-Nov-13 |      |     | █   | █   |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 60      | 17-Dec-13 | 23-Jan-14 |      |     |     |     | █    | █   |     |     |     |     |     |     |      |     |     |     |      |
| 70      | 24-Jan-14 | 23-Mar-14 |      |     |     |     |      | █   | █   | █   |     |     |     |     |      |     |     |     |      |
| 80      | 17-Dec-13 | 31-Dec-13 |      |     |     |     | █    |     |     |     |     |     |     |     |      |     |     |     |      |
| 90      | 17-Dec-13 | 23-Jan-14 |      |     |     |     | █    | █   |     |     |     |     |     |     |      |     |     |     |      |
| 100     | 24-Jan-14 | 23-Mar-14 |      |     |     |     |      | █   | █   | █   |     |     |     |     |      |     |     |     |      |
| 110     | 17-Dec-13 | 7-Apr-14  |      |     |     |     | █    | █   | █   | █   |     |     |     |     |      |     |     | █   |      |
| 120     | 24-Mar-14 | 2-Nov-14  |      |     |     |     |      |     |     | █   | █   | █   | █   | █   | █    | █   | █   | █   |      |
| 130     | 11-Nov-13 | 29-Nov-13 |      |     | █   |     |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 132     | 30-Nov-13 | 2-Dec-13  |      |     |     | █   |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 134     | 3-Dec-13  | 2-Jan-14  |      |     |     |     | █    | █   |     |     |     |     |     |     |      |     |     |     |      |
| 136     | 3-Jan-14  | 9-Mar-14  |      |     |     |     |      | █   | █   | █   |     |     |     |     |      |     |     |     |      |
| 140     | 30-Sep-13 | 2-Nov-13  |      | █   | █   |     |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 143     | 4-Nov-13  | 9-Nov-13  |      |     | █   |     |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 147     | 25-Oct-13 | 9-Nov-13  |      |     | █   |     |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 148     | 11-Nov-13 | 23-Nov-13 |      |     | █   |     |      |     |     |     |     |     |     |     |      |     |     |     |      |
| 150     | 25-Nov-13 | 10-Dec-13 |      |     |     | █   | █    |     |     |     |     |     |     |     |      |     |     |     |      |
| 160     | 11-Dec-13 | 10-Jan-14 |      |     |     |     | █    | █   |     |     |     |     |     |     |      |     |     |     |      |
| 170     | 18-Nov-14 | 21-Dec-14 |      |     |     |     |      |     |     |     |     |     |     |     |      |     |     | █   | █    |
| 180     | 23-Dec-14 | 5-Jan-15  |      |     |     |     |      |     |     |     |     |     |     |     |      |     |     |     | █    |

 Non-critical Activity  
 Critical Activity

---

---

**APPENDIX C  
IMPLEMENTATION SCHEDULE OF  
ENVIRONMENTAL MITIGATION MEASURES  
(EMIS)**

---

---

**Appendix C - Implementation Schedule of Environmental Mitigation Measures (EMIS)**

Air Quality - Schedule of Recommended Mitigation Measures

| Impact                          | Mitigation Measures                                                                                                                                                                                                                                                                                                                                                | Timing              | Implementation Status |        |        |
|---------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-----------------------|--------|--------|
|                                 |                                                                                                                                                                                                                                                                                                                                                                    |                     | Jul 14                | Aug 14 | Sep 14 |
| Air Quality during Construction | <ul style="list-style-type: none"> <li>Careful siting of construction activities which generate substantial amount of dust can effectively reduce the overall impact.</li> </ul>                                                                                                                                                                                   | During construction | V                     | V      | @      |
|                                 | <ul style="list-style-type: none"> <li>Use of regular watering, with complete coverage if possible, to reduce dust emissions from exposed site surfaces and unpaved roads and for dusty construction areas and areas close to ASRs, particularly during dry weather.</li> </ul>                                                                                    |                     | V                     | V      | V      |
|                                 | <ul style="list-style-type: none"> <li>Open stockpiles shall be avoided. Side enclosure and covering of any aggregate or dusty material storage piles to reduce emissions. Where possible, prevent placing dusty material storage piles near ASRs. Where this is not practicable owing to frequent usage, watering shall be applied to aggregate fines.</li> </ul> |                     | V                     | V      | @      |
|                                 | <ul style="list-style-type: none"> <li>No free falling construction debris should be allowed; debris should be let down by hoist or enclosed tunnel to the ground.</li> </ul>                                                                                                                                                                                      |                     | N/A                   | N/A    | N/A    |
|                                 | <ul style="list-style-type: none"> <li>All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet.</li> </ul>                                                                                                                                                                |                     | V                     | V      | V      |
|                                 | <ul style="list-style-type: none"> <li>Provision of wind shield and dust extraction units or similar dust mitigation measures at the loading points, and use of water sprinklers at the loading area where dust generation is likely during the loading process of loose material, particularly in dry seasons/ periods.</li> </ul>                                |                     | V                     | V      | V      |
|                                 | <ul style="list-style-type: none"> <li>Height from which dusty materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading.</li> </ul>                                                                                                                                                               |                     | N/A                   | N/A    | N/A    |
|                                 | <ul style="list-style-type: none"> <li>Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.</li> </ul>                                                                                                                                                                                                                   |                     | V                     | V      | V      |
|                                 | <ul style="list-style-type: none"> <li>Skip hoist for material transport should be totally enclosed by impervious sheeting.</li> </ul>                                                                                                                                                                                                                             |                     | V                     | V      | V      |
|                                 | <ul style="list-style-type: none"> <li>Establishment and use of vehicle wheel and body washing facilities at the exit points of the site and public roads, combined with cleaning of public roads wherever necessary and practical.</li> </ul>                                                                                                                     |                     | V                     | V      | V      |
|                                 | <ul style="list-style-type: none"> <li>The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores.</li> </ul>                                                                                                                       |                     | V                     | V      | V      |
|                                 | <ul style="list-style-type: none"> <li>Provision of not less than 2.4m high hoarding from ground level along site boundary where adjoins a road, streets or other accessible to the public except for a site entrance or exit.</li> </ul>                                                                                                                          |                     | V                     | V      | V      |

| Impact                          | Mitigation Measures                                                                                                                                                                                                                                            | Timing              | Implementation Status |        |        |
|---------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-----------------------|--------|--------|
|                                 |                                                                                                                                                                                                                                                                |                     | Jul 14                | Aug 14 | Sep 14 |
| Air Quality during Construction | <ul style="list-style-type: none"> <li>Imposition of speed controls for vehicles on site haul roads. Where feasible, routing of vehicles and positioning of construction plants should be at a maximum possible distances from sensitive receivers.</li> </ul> | During construction | V                     | V      | V      |
|                                 | <ul style="list-style-type: none"> <li>Every stock of more than 20 bags of cement or dry pulverised fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides.</li> </ul>                     |                     | N/A                   | N/A    | N/A    |
|                                 | <ul style="list-style-type: none"> <li>Instigation of an environmental monitoring and auditing program to monitor the construction process in order to enforce controls and modify method of work if dusty conditions arise.</li> </ul>                        |                     | V                     | V      | V      |

Noise - Schedule of Recommended Mitigation Measures

| Impact                                 | Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                                                       | Timing                                          | Implementation Status |        |        |
|----------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------|-----------------------|--------|--------|
|                                        |                                                                                                                                                                                                                                                                                                                                                                                                                                                           |                                                 | Jul 14                | Aug 14 | Sep 14 |
| Construction Noise during Construction | <ul style="list-style-type: none"> <li>In order to reduce the excessive noise impacts at the affected NSRs during normal daytime working hours, the following mitigation measures shall be implemented:- <ul style="list-style-type: none"> <li>adopting quiet powered mechanical equipment;</li> <li>scheduling of works;</li> <li>erect a 3m tall moveable noise barriers along the site boundary; and</li> <li>noise enclosure.</li> </ul> </li> </ul> | During construction                             | @                     | V      | V      |
|                                        | <ul style="list-style-type: none"> <li>Only well-maintained plant should be operated on-site and plant should be serviced regularly.</li> </ul>                                                                                                                                                                                                                                                                                                           |                                                 | V                     | V      | V      |
|                                        | <ul style="list-style-type: none"> <li>Silencers or mufflers on construction equipment should be utilized and should be properly maintained.</li> </ul>                                                                                                                                                                                                                                                                                                   |                                                 | V                     | V      | V      |
|                                        | <ul style="list-style-type: none"> <li>Mobile plant, if any, should be sited as far away from NSRs as possible.</li> </ul>                                                                                                                                                                                                                                                                                                                                |                                                 | V                     | V      | V      |
|                                        | <ul style="list-style-type: none"> <li>Machines and plant (such as trucks) that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum.</li> </ul>                                                                                                                                                                                                                                                 |                                                 | V                     | V      | V      |
|                                        | <ul style="list-style-type: none"> <li>Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.</li> </ul>                                                                                                                                                                                                                                                   |                                                 | V                     | V      | V      |
|                                        | <ul style="list-style-type: none"> <li>Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>                                                                                                                                                                                                                                                 |                                                 | V                     | V      | V      |
|                                        | <ul style="list-style-type: none"> <li>Use of acoustic barriers as close to the source as possible. Equipment to be shielded: air compressor, water pump, concrete pump, dumper, dump truck, generator, various hand tools, saw, excavator, loader, truck mixer, mobile crane, vibrator and breaker.</li> </ul>                                                                                                                                           | During examination periods of the school nearby | V                     | V      | V      |

Water Quality - Schedule of Recommended Mitigation Measures

| Impact                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | Timing              | Implementation Status |        |        |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-----------------------|--------|--------|
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              |                     | Jul 14                | Aug 14 | Sep 14 |
| Water Quality during Construction                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | <b>Construction works at or close to the seafront</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |                     |                       |        |        |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | <ul style="list-style-type: none"> <li>Temporary storage of construction materials (e.g. equipment, filling materials, chemicals and fuel), chemical waste storage area and temporary stockpile of construction and demolition materials should be located well away from the seawater front and storm drainage during carrying out of the works.</li> </ul>                                                                                                                                                                                 | During construction | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | <ul style="list-style-type: none"> <li>Stockpiling of construction and demolition materials and dusty materials should be covered and located away from the seawater front and storm drainage.</li> </ul>                                                                                                                                                                                                                                                                                                                                    |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | <ul style="list-style-type: none"> <li>Construction debris and spoil should be covered up and/or disposed of as soon as possible to avoid being washed into the nearby receiving waters.</li> </ul>                                                                                                                                                                                                                                                                                                                                          |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | <b>Construction run-off and Drainage</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |                     |                       |        |        |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | <p>The site practices outlined in ProPECC PN 1/94 "Construction Site Drainage" shall be followed as far as practicable in order to minimise surface runoff and the chance of erosion, and also to retain and reduce any suspended solids prior to discharge. These practices include, inter alia, the following items:-</p> <ul style="list-style-type: none"> <li>Provision of perimeter channels to intercept storm-runoff from outside the site. These shall be constructed in advance of site formation works and earthworks.</li> </ul> | During construction | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | <ul style="list-style-type: none"> <li>Vehicle and plant servicing areas, vehicle wash bays and lubrication bays should as far as possible be located within roofed areas. The drainage in these covered areas should be connected to foul sewers via a petrol interceptor and/or oil/grease separator. Oil leakage or spillage should be contained and cleaned up immediately. Waste oil should be collected and stored for recycling or disposal in accordance with the Waste Disposal Ordinance.</li> </ul>                               |                     | V                     | V      | V      |
| <ul style="list-style-type: none"> <li>Sand/silt removal facilities such as sand traps, silt traps and sediment basins shall be provided to remove sand/silt particles from runoff to meet the requirements of the Technical Memorandum standard under the Water Pollution Control Ordinance. The design of silt removal facilities should be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures should be inspected monthly, regularly cleaned and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.</li> </ul> |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | V                   | V                     | V      |        |

| Impact                                                                                                                                                                                                                                                                                                                        | Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                           | Timing              | Implementation Status |        |        |  |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-----------------------|--------|--------|--|
|                                                                                                                                                                                                                                                                                                                               |                                                                                                                                                                                                                                                                                                                                                                                                               |                     | Jul 14                | Aug 14 | Sep 14 |  |
| Water Quality during Construction                                                                                                                                                                                                                                                                                             | <ul style="list-style-type: none"> <li>Careful programming of the works to minimise the potential of soil erosion during the rainy season. Other measures that need to be implemented before, during, and after rainstorms are summarized in ProPECC PN 1/94.</li> </ul>                                                                                                                                      | During construction | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                               | <ul style="list-style-type: none"> <li>Exposed soil surface shall be protected by paving as soon as possible to reduce the potential of soil erosion.</li> </ul>                                                                                                                                                                                                                                              |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                               | <ul style="list-style-type: none"> <li>Open stockpiles of construction materials on site shall be covered with tarpaulin or similar fabric during rainstorm.</li> </ul>                                                                                                                                                                                                                                       |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                               | <b>General Construction Activities</b>                                                                                                                                                                                                                                                                                                                                                                        |                     |                       |        |        |  |
|                                                                                                                                                                                                                                                                                                                               | <ul style="list-style-type: none"> <li>Debris and rubbish generated on-site shall be collected, handled and disposed of properly to avoid entering the nearby nullah and stormwater drains. Stockpiles of cement and other construction material should be kept covered when not being used.</li> </ul>                                                                                                       | During construction | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                               | <ul style="list-style-type: none"> <li>Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. All fuel tanks and storage areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event.</li> </ul> |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                               | <b>Sewage Effluent</b>                                                                                                                                                                                                                                                                                                                                                                                        |                     |                       |        |        |  |
|                                                                                                                                                                                                                                                                                                                               | <ul style="list-style-type: none"> <li>Temporary sanitary facilities, such as portable chemical toilets, shall be employed on-site. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities.</li> </ul>                                                                                                                                                       | During construction | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                               | <ul style="list-style-type: none"> <li>Effluent discharged from the construction site should comply with the standards stipulated in the TM-DSS.</li> </ul>                                                                                                                                                                                                                                                   |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                               | <ul style="list-style-type: none"> <li>Subject to the sampling results of Contamination Assessment Plan of the site, any contaminated land treatments are subjected to EPD's requirements on handling, treatment and disposal. Should effluent stream and/or extracted ground water be discharged from the site, the discharge shall comply with the WPCO and any EPD special requirements.</li> </ul>        |                     | N/A                   | N/A    | N/A    |  |
| <ul style="list-style-type: none"> <li>Establishment of baseline and impact monitoring program to establish the baseline water quality condition and monitor the construction process in order to enforce controls and modify method of work if any adverse impacts on the water sensitive receivers are detected.</li> </ul> | V                                                                                                                                                                                                                                                                                                                                                                                                             |                     | V                     | V      |        |  |

Waste Management- Schedule of Recommended Mitigation Measures

| Impact                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             | Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                 | Timing              | Implementation Status |        |        |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-----------------------|--------|--------|
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |                                                                                                                                                                                                                                                                                                                                                                                     |                     | Jul 14                | Aug 14 | Sep 14 |
| Waste Management during Construction                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | <b>Good Site Practice</b>                                                                                                                                                                                                                                                                                                                                                           |                     |                       |        |        |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>Nominate an approved personnel, such as a site manager, to be responsible for good site practices and effective arrangements for collection and disposal to an appropriate facility of all wastes generated at the works area. Training of site personnel in proper waste management and handling procedures shall be undertaken.</li> </ul> | During construction | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>Construction materials should be planned and stocked carefully to minimise and avoid unnecessary generation of waste.</li> </ul>                                                                                                                                                                                                             |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>General refuse shall be stored and collected separately from other construction and chemical wastes. Provide on-site refuse collection facilities and enclosed transfer facility for storage and containment.</li> </ul>                                                                                                                     |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>Waste points should be provided sufficiently and waste should be collected regularly.</li> </ul>                                                                                                                                                                                                                                             |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.</li> </ul>                                                                                                                                                             |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>Separate chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Centre located at Tsing Yi. Chemical waste shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.</li> </ul>                                                                 |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.</li> </ul>                                                                                                                                                                                                                                      |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>Develop procedures such as a trip-ticket system to monitor the disposal of C&amp;D material and solid wastes at public filling areas and landfills, and to control fly-tipping.</li> </ul>                                                                                                                                                   |                     | V                     | V      | V      |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>A recording system for the amount of wastes generated, recycled and disposed should be proposed.</li> </ul>                                                                                                                                                                                                                                  |                     | V                     | V      | V      |
| <b>Waste Reduction Measures</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |                                                                                                                                                                                                                                                                                                                                                                                     |                     |                       |        |        |
| <p>Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:-</p> <ul style="list-style-type: none"> <li>Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> </ul> | During construction                                                                                                                                                                                                                                                                                                                                                                 | V                   | V                     | V      |        |



| Impact                                                                                                                                                                                                                                                                                                                                                       | Mitigation Measures                                                                                                                                                                                                                                                                               | Timing              | Implementation Status |        |        |  |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-----------------------|--------|--------|--|
|                                                                                                                                                                                                                                                                                                                                                              |                                                                                                                                                                                                                                                                                                   |                     | Jul 14                | Aug 14 | Sep 14 |  |
| Waste Management during Construction                                                                                                                                                                                                                                                                                                                         | <ul style="list-style-type: none"> <li>Encourage collection of aluminum cans, PET bottles and paper by providing separate labelled bins to enable these wastes to be segregated from other general refuse generated by the work force.</li> </ul>                                                 | During construction | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>Any unused chemicals or those with remaining functional capacity shall be recycled.</li> </ul>                                                                                                                                                             |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>Use of reusable non-timber formwork to reduce the amount of C&amp;D material.</li> </ul>                                                                                                                                                                   |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>Prior to disposal of C&amp;D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill.</li> </ul>                                       |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> </ul>                                                                                                                              |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> </ul>                                                                                                                |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <b>General Site Wastes</b>                                                                                                                                                                                                                                                                        |                     |                       |        |        |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>Collection area for construction site waste should be provided where waste can be stored prior to removal from site.</li> </ul>                                                                                                                            | During construction | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>An enclosed and covered area for the collection of the waste is recommended to reduce 'wind blow' of light material.</li> </ul>                                                                                                                            |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>An open area used for storage or loading/unloading of wastes should be bunded and all the polluted surface run-off collected within this area should be diverted into sewers.</li> </ul>                                                                   |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>General refuse should be stored in enclosed bins or compaction units separate from C&amp;D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&amp;D material.</li> </ul> |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <b>Workforce Wastes</b>                                                                                                                                                                                                                                                                           |                     |                       |        |        |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>Suitable collection sites around site offices and canteen should be required.</li> </ul>                                                                                                                                                                   | During construction | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                              | <ul style="list-style-type: none"> <li>Waste should be removed daily or as often as required.</li> </ul>                                                                                                                                                                                          |                     | V                     | V      | V      |  |
| <b>Chemical Waste</b>                                                                                                                                                                                                                                                                                                                                        |                                                                                                                                                                                                                                                                                                   |                     |                       |        |        |  |
| <ul style="list-style-type: none"> <li>After use, chemical waste (for example, cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Package, Labelling and Storage of Chemical Wastes.</li> </ul>                                                                                                 | During construction                                                                                                                                                                                                                                                                               | V                   | V                     | V      |        |  |
| <ul style="list-style-type: none"> <li>Waste should be properly stored on site within suitably designed containers and should be collected by approved licensed waste collectors for disposal at the Chemical Waste Treatment Centre (CWTC) or other licensed facility in accordance with the Waste Disposal Chemical Waste (General) Regulation.</li> </ul> |                                                                                                                                                                                                                                                                                                   | V                   | V                     | V      |        |  |

| Impact                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Mitigation Measures                                                                                                                                                                                                                                                                                                 | Timing              | Implementation Status |        |        |  |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-----------------------|--------|--------|--|
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         |                                                                                                                                                                                                                                                                                                                     |                     | Jul 14                | Aug 14 | Sep 14 |  |
| Waste Management during Construction                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>Any service shop and minor maintenance facilities should be located on hard standing within a bunded area, and sumps and oil interceptors should be provided.</li> </ul>                                                                                                     | During construction | N/A                   | N/A    | N/A    |  |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | <ul style="list-style-type: none"> <li>Provision of appropriate on-site temporary storage facility for any asbestos containing materials (ACM) where necessary. Storage facilities shall be designed in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.</li> </ul> |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | <ul style="list-style-type: none"> <li>Employ registered contractors for removal of ACM off-site and disposal at a designated landfill site.</li> </ul>                                                                                                                                                             |                     | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | <b>Construction and Demolition Material</b>                                                                                                                                                                                                                                                                         |                     |                       |        |        |  |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | <ul style="list-style-type: none"> <li>The selective demolition method is recommended to be employed to minimize the effort of sorting mixed C&amp;D materials.</li> </ul>                                                                                                                                          | During construction | V                     | V      | V      |  |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | <ul style="list-style-type: none"> <li>In order to minimise the impact resulting from collection and transportation of C&amp;D material for off-site disposal, it is recommended that the public fill material generated from demolition works shall be re-used on-site as far as possible.</li> </ul>              |                     | V                     | V      | V      |  |
| <ul style="list-style-type: none"> <li>A suitable area should be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials. Separate construction and demolition material into C&amp;D waste (non-inert material) and public fill (inert material) for appropriate disposal. Public fill disposed at a public filling area shall only consist of earth, building debris, broken rock and concrete. The material shall be free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered to be unsuitable by the Filling Supervisor. Small quantities of timber mixed with otherwise suitable material would be permitted. C&amp;D waste, such as wood, glass, plastic, steel and other metals, shall be reused or recycled and, as a last resort, disposed to landfill.</li> </ul> | V                                                                                                                                                                                                                                                                                                                   |                     | V                     | V      |        |  |

Land Contamination - Schedule of Recommended Mitigation Measures

| Impact                                                                                                                                                            | Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Timing                                                                                                                                                                                                                                                                                                                                                                                                                                      | Implementation Status                                                                                                                                                                                                                                                                 |                                                                                                                                                                                                                                                                                       |                                                                                                                                                                                                                                                                                       |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                                                                                                                                                   |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |                                                                                                                                                                                                                                                                                                                                                                                                                                             | Jul 14                                                                                                                                                                                                                                                                                | Aug 14                                                                                                                                                                                                                                                                                | Sep 14                                                                                                                                                                                                                                                                                |
| Land Contamination (For inaccessible lots and lots which the Permit Holder opt to re-assess in accordance with the Risk-Based Remediation Goals (RBRGs) approach) | <ul style="list-style-type: none"> <li>Further land contamination assessments to be carried out for inaccessible lots, lots which the Permit Holder opt to re-assess in accordance with the RBRGs approach, as well as areas that required further sampling to ascertain contamination extent. Supplementary CAP, CAR and RAPs to be submitted to EPD for endorsement before commencement of remediation work. These reports shall detail the further sampling &amp; remediation works required. The development construction work shall only commence after all the remediation work has been completed.</li> </ul> | <p>Inaccessible lots as described under para. 3.5 of Appendix 7A of YTB-EIA as well as areas that required further sampling to ascertain contamination extent/ Upon availability of site access</p> <p>Supplementary CAP, CAR and RAPs to be submitted to EPD for endorsement before commencement of the remediation work.</p> <p>Development construction work should only commence after all the remediation work has been completed.</p> | <p>V</p> <p>(Two CAPs (Yau Tong Bay - Decommissioning of Shipyard Sites Supplementary CAP for Previous Inaccessible Lots (YTML 27, 44, 45-46, 54 and Underground Oil Tank at YTML 6-11) &amp; Yau Tong Bay - Decommissioning of Shipyard Sites (CAP for YTML 1, 6-11, 15, 28, 29,</p> | <p>V</p> <p>(Two CAPs (Yau Tong Bay - Decommissioning of Shipyard Sites Supplementary CAP for Previous Inaccessible Lots (YTML 27, 44, 45-46, 54 and Underground Oil Tank at YTML 6-11) &amp; Yau Tong Bay - Decommissioning of Shipyard Sites (CAP for YTML 1, 6-11, 15, 28, 29,</p> | <p>V</p> <p>(Two CAPs (Yau Tong Bay - Decommissioning of Shipyard Sites Supplementary CAP for Previous Inaccessible Lots (YTML 27, 44, 45-46, 54 and Underground Oil Tank at YTML 6-11) &amp; Yau Tong Bay - Decommissioning of Shipyard Sites (CAP for YTML 1, 6-11, 15, 28, 29,</p> |

| Impact                                             | Mitigation Measures                                                                                                                                                                                                                                                               | Timing                                                                                                                                          | Implementation Status                                                                                                                                                                                                                            |                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                  |
|----------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                                    |                                                                                                                                                                                                                                                                                   |                                                                                                                                                 | Jul 14                                                                                                                                                                                                                                           | Aug 14                                                                                                                                                                                                                                           | Sep 14                                                                                                                                                                                                                                           |
|                                                    |                                                                                                                                                                                                                                                                                   |                                                                                                                                                 | 38 and 41-43)) have been submitted to EPD and approved on 6 Jul 2011 and 30 Aug 2011 respectively. The corresponding CARs and RAPs were submitted to EPD in June 2012 and were subsequently approved in June 2013 after two rounds of comment .) | 38 and 41-43)) have been submitted to EPD and approved on 6 Jul 2011 and 30 Aug 2011 respectively. The corresponding CARs and RAPs were submitted to EPD in June 2012 and were subsequently approved in June 2013 after two rounds of comment .) | 38 and 41-43)) have been submitted to EPD and approved on 6 Jul 2011 and 30 Aug 2011 respectively. The corresponding CARs and RAPs were submitted to EPD in June 2012 and were subsequently approved in June 2013 after two rounds of comment .) |
| Land Contamination (For inaccessible lots and lots | <ul style="list-style-type: none"> <li>A method statement detailing the following shall be submitted to EPD for endorsement:- <ul style="list-style-type: none"> <li>Methodology, monitoring and verification procedures for biopiling and solidification;</li> </ul> </li> </ul> | All areas identified to require solidification of soil as land remediation / The pilot test results and method statement shall be submitted and | V<br><br>(A method                                                                                                                                                                                                                               | V<br><br>(A method                                                                                                                                                                                                                               | V<br><br>(A method                                                                                                                                                                                                                               |

| Impact                                                                                                                                                            | Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            | Timing                                                                                                                                                                                                                                                                                | Implementation Status                                                                                                                               |                                                                                                                                                     |                                                                                                                                                     |
|-------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------|
|                                                                                                                                                                   |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                                                                                                                                                                       | Jul 14                                                                                                                                              | Aug 14                                                                                                                                              | Sep 14                                                                                                                                              |
| which the Permit Holder opt to re-assess in accordance with the Risk-Based Remediation Goals (RBRGs) approach)                                                    | <ul style="list-style-type: none"> <li>- Pilot test procedures for solidification process to ascertain the concrete mix recipe and leachability of the product;</li> <li>- The sample size for the verification soil test to be conducted by IEA for spot check purpose;</li> <li>- The notification system for notifying the Director the satisfactory completion of the excavation and treatment of contaminated soil; and</li> <li>- Provision and operation requirements of equipment and personnel decontamination facilities.</li> </ul> | <p>endorsed at least one month prior to the full scale solidification works.</p> <p>All soil identified and to be identified as contaminated with TPH / The method statement shall be submitted and endorsed at least one month prior to the commencement of the biopiling works.</p> | <p>statement for biopiling and solidification has been submitted to EPD on 2 Oct 2013. The method statement is endorsed by EPD on 20 Dec 2013.)</p> | <p>statement for biopiling and solidification has been submitted to EPD on 2 Oct 2013. The method statement is endorsed by EPD on 20 Dec 2013.)</p> | <p>statement for biopiling and solidification has been submitted to EPD on 2 Oct 2013. The method statement is endorsed by EPD on 20 Dec 2013.)</p> |
| Land Contamination (For inaccessible lots and lots which the Permit Holder opt to re-assess in accordance with the Risk-Based Remediation Goals (RBRGs) approach) | <ul style="list-style-type: none"> <li>• A Soil Remediation Report should be submitted to EPD to demonstrate that the remediation work has been properly carried out.</li> </ul>                                                                                                                                                                                                                                                                                                                                                               | <p>All areas identified to require soil and groundwater remediation / The Remediation Report shall be submitted and endorsed prior to the commencement of the development construction works.</p>                                                                                     | N/A                                                                                                                                                 | N/A                                                                                                                                                 | <p>@</p> <p>(The batch 1 of Soil Remediation Report [SRR for YTML 1, 5, 6-11, 12, 13-14, 54, 19-21, 22A, 22B, 22RP and 23-24</p>                    |

| Impact                                                                                                                                                                                             | Mitigation Measures                                                                                                                                                                                                                                                                                                                                                                                                             | Timing                                                                                                                                                                                                 | Implementation Status                                                                                      |                                                                                                            |                                                                                                            |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------|
|                                                                                                                                                                                                    |                                                                                                                                                                                                                                                                                                                                                                                                                                 |                                                                                                                                                                                                        | Jul 14                                                                                                     | Aug 14                                                                                                     | Sep 14                                                                                                     |
|                                                                                                                                                                                                    |                                                                                                                                                                                                                                                                                                                                                                                                                                 |                                                                                                                                                                                                        |                                                                                                            |                                                                                                            | (Zone nos. T19A, T22BA, T22BB, A1, R5, R6]] has been submitted to EPD on 18 August 2014.)                  |
|                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>• Inspections for dioxin. Should there be signs of incineration facilities, burn pits or facilities that utilises high temperature burning, soil sampling for dioxin will be carried out. Details regarding such sampling shall be approved by EPD. A detailed proposal for dealing with dioxin contaminated material, if found, shall also be submitted to EPD for approval.</li> </ul> | All the Yau Tong Bay marine lots inspection and testing shall commence upon availability of site.                                                                                                      | V                                                                                                          | V                                                                                                          | V                                                                                                          |
| Land Contamination (For lots and facilities assessed under EIA with approved CAP, CAR and RAP based on Dutch B levels referenced to ProPECC PN3/94 – Contaminated Land Assessment and Remediation) | <ul style="list-style-type: none"> <li>• A pilot test shall be conducted to ascertain the concrete mix recipe and leachability of the product prior to a full scale solidification and a method statement detailing the solidification procedure (including the sampling proposal for process monitoring) shall be submitted to EPD for endorsement.</li> </ul>                                                                 | All areas identified to require solidification of soil as land remediation / The pilot test results and method statement shall be submitted and endorsed prior to the full scale solidification works. | V<br>(A pilot test to ascertain the concrete mix recipe was conducted on 30 Dec 2013. The method statement | V<br>(A pilot test to ascertain the concrete mix recipe was conducted on 30 Dec 2013. The method statement | V<br>(A pilot test to ascertain the concrete mix recipe was conducted on 30 Dec 2013. The method statement |

| Impact                                                                                                                                                                                             | Mitigation Measures                                                                                                                                                                         | Timing                                                                                                                                                                     | Implementation Status                                                                                                                  |                                                                                                                                        |                                                                                                                                        |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------|
|                                                                                                                                                                                                    |                                                                                                                                                                                             |                                                                                                                                                                            | Jul 14                                                                                                                                 | Aug 14                                                                                                                                 | Sep 14                                                                                                                                 |
|                                                                                                                                                                                                    |                                                                                                                                                                                             |                                                                                                                                                                            | t for solidification has been submitted to EPD on 2 Oct 2013 and subsequently endorsed by EPD on 20 Dec 2013.)                         | t for solidification has been submitted to EPD on 2 Oct 2013 and subsequently endorsed by EPD on 20 Dec 2013.)                         | t for solidification has been submitted to EPD on 2 Oct 2013 and subsequently endorsed by EPD on 20 Dec 2013.)                         |
| Land Contamination (For lots and facilities assessed under EIA with approved CAP, CAR and RAP based on Dutch B levels referenced to ProPECC PN3/94 – Contaminated Land Assessment and Remediation) | <ul style="list-style-type: none"> <li>A method statement detailing the biopiling methodology, monitoring and verification procedures shall be submitted to EPD for endorsement.</li> </ul> | All soil identified and to be identified as contaminated with TPH / The method statement shall be submitted and endorsed prior to the commencement of the biopiling works. | V<br><br>(The method statement for biopiling has been submitted to EPD on 2 Oct 2013 and subsequently endorsed by EPD on 20 Dec 2013.) | V<br><br>(The method statement for biopiling has been submitted to EPD on 2 Oct 2013 and subsequently endorsed by EPD on 20 Dec 2013.) | V<br><br>(The method statement for biopiling has been submitted to EPD on 2 Oct 2013 and subsequently endorsed by EPD on 20 Dec 2013.) |
|                                                                                                                                                                                                    | <ul style="list-style-type: none"> <li>A Soil Remediation Report should be submitted to EPD to demonstrate that the remediation work has been properly carried out.</li> </ul>              | All areas identified to require soil and groundwater remediation / The Remediation Report shall be submitted and endorsed prior to the commencement of the development     | N/A                                                                                                                                    | N/A                                                                                                                                    | @<br><br>(The batch 1 of Soil                                                                                                          |

| Impact | Mitigation Measures | Timing              | Implementation Status |        |                                                                                                                                                                                       |
|--------|---------------------|---------------------|-----------------------|--------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|        |                     |                     | Jul 14                | Aug 14 | Sep 14                                                                                                                                                                                |
|        |                     | construction works. |                       |        | Remediation Report [SRR for YTML 1, 5, 6-11, 12, 13-14, 54, 19-21, 22A, 22B, 22RP and 23-24 (Zone nos. T19A, T22BA, T22BB, A1, R5, R6)] has been submitted to EPD on 18 August 2014.) |

Landscape and Visual Impact - Schedule of Recommended Mitigation Measures

| Impact               | Mitigation Measures                                                                                                                                                                                | Timing              | Implementation Status |        |        |
|----------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-----------------------|--------|--------|
|                      |                                                                                                                                                                                                    |                     | Jul 14                | Aug 14 | Sep 14 |
| Landscape and Visual | <ul style="list-style-type: none"> <li>On-site mature trees within the Project boundary shall be retained. Any mature tree shall not be transplanted or fell unless permission has been</li> </ul> | During construction | V                     | V      | V      |



|                            |                                                                                            |  |   |   |   |
|----------------------------|--------------------------------------------------------------------------------------------|--|---|---|---|
| Impact during Construction | given by EPD.                                                                              |  |   |   |   |
|                            | • During the biopiling process, the biopiles shall be limited to a height of less than 3m. |  | V | V | V |
|                            | • Erection and maintenance of decorative screen/colour hoarding around the site.           |  | V | V | V |

Legend: V = implemented;

X = not implemented;

@ = partially implemented;

N/A = not applicable - No such work was undertaken or no such material was used on site.

---

---

**APPENDIX D  
SUMMARY OF ACTION AND LIMIT LEVELS**

---

---

## Appendix D - Summary of Action and Limit Levels

Table 1 – Action and Limit Levels for Construction Noise (0700-1900 hrs of normal weekdays)




| <b>Location</b> | <b>Action Level</b>                                                                                                                  | <b>Limit Level</b> |
|-----------------|--------------------------------------------------------------------------------------------------------------------------------------|--------------------|
| NM1             | When one documented complaint, related to 0700 – 1900 hours on normal weekdays, is received from any one of the sensitive receivers. | 75 dB(A)           |
| NM2             |                                                                                                                                      | 65/70 dB(A)*       |
| NM3             |                                                                                                                                      | 65/70 dB(A)*       |

\*Daytime noise Limit Level of 70 dB(A) applies to education institutions, while 65dB(A) applies during school examination period.

---

**APPENDIX E  
GRAPHICAL PRESENTATION OF IMPACT  
DAYTIME CONSTRUCTION NOISE  
MONITORING RESULTS OVER PAST FOUR  
MONTHS**

---

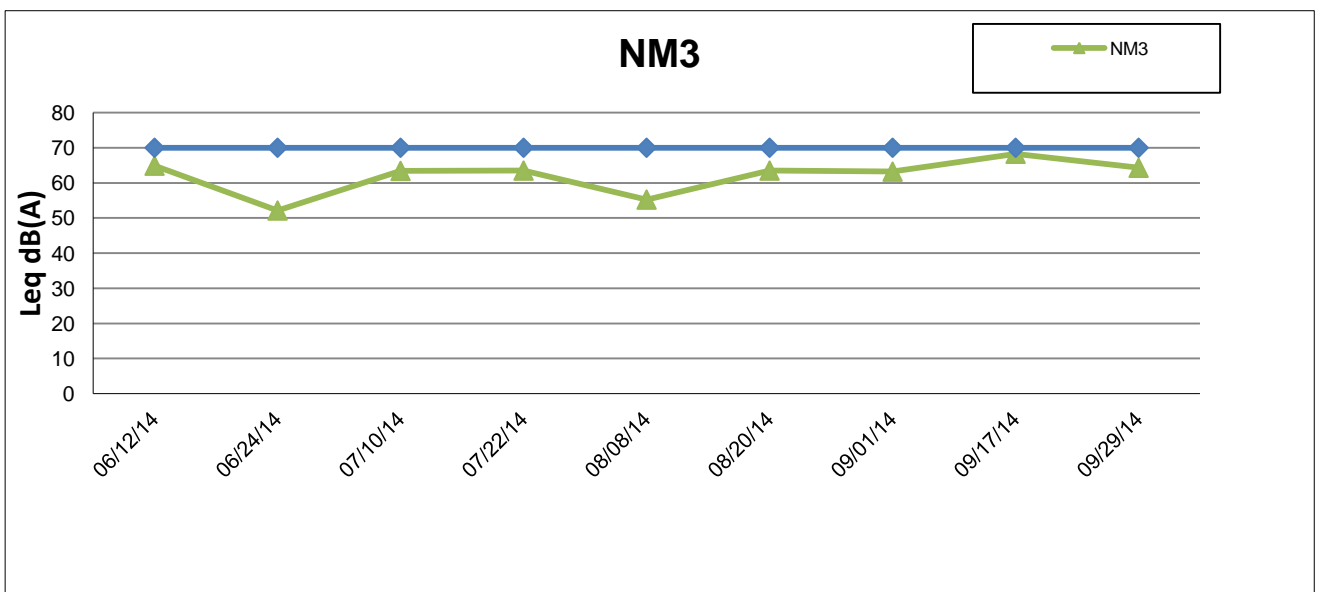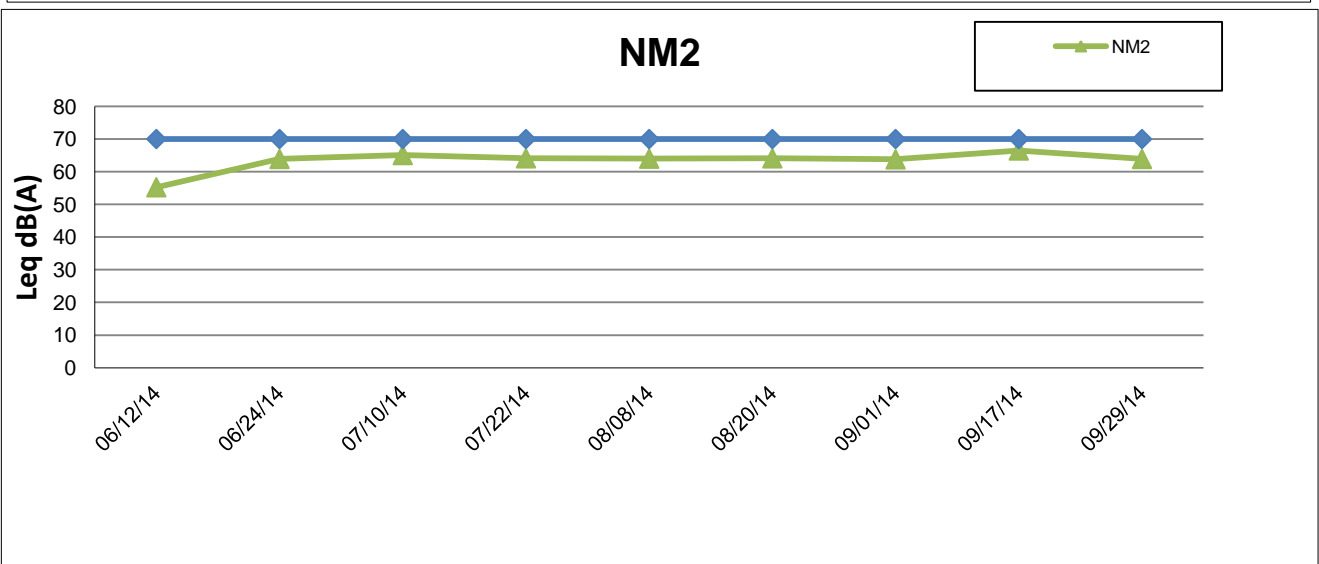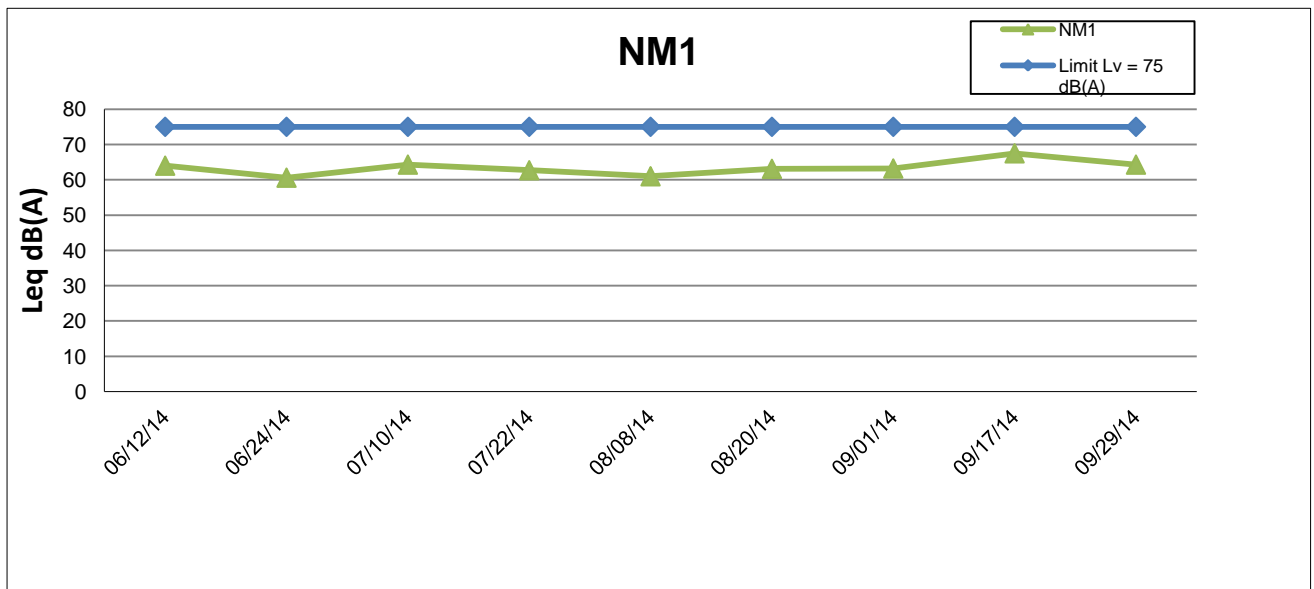

**Remark:** Measured noise level would be shown if Measured noise level (Leq) <= Baseline noise level

|              |                                                                                       |         |          |              |        |
|--------------|---------------------------------------------------------------------------------------|---------|----------|--------------|--------|
| <b>AECOM</b> | <b>Yau Tong Bay – Decommissioning of Shipyard Sites</b>                               | SCALE   | N.T.S.   | DATE         | Oct-14 |
|              | <b>Graphical Presentation of Impact Daytime Construction Noise Monitoring Results</b> | CHECK   | ENFL     | DRAWN        | OLWY   |
|              |                                                                                       | JOB NO. | 60048283 | APPENDIX No. | G      |
|              |                                                                                       |         |          |              | -      |

---

---

**APPENDIX F  
STATISTICS ON COMPLAINTS,  
NOTIFICATION OF SUMMONS AND  
SUCCESSFUL PROSECUTIONS**

---

---

## Appendix F

### Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

|                                 | Date Received                        | Subject                                                                                                                                                                                                                                                | Status | Total no. in this reporting quarter | Total no. since project commencement |
|---------------------------------|--------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------|-------------------------------------|--------------------------------------|
| <b>Environmental complaints</b> | 3 August 2012<br>(Referred from EPD) | Concern of air emission from the spraying activities carried out at the construction site near the junction of Ko Fai Road and Cha Kwo Ling Road on 3 August 2012 that would stain the bodies of vehicles nearby and cause air nuisance to the public. | Closed | 1                                   | 4                                    |
| <b>Notification of summons</b>  | -                                    | -                                                                                                                                                                                                                                                      | -      | 0                                   | 0                                    |
| <b>Successful Prosecutions</b>  | -                                    | -                                                                                                                                                                                                                                                      | -      | 0                                   | 0                                    |
