




Contract No. YL/2013/01

Cycle Tracks from Tuen Mun to Sheung Shui- Stage 1

Environmental Monitoring and Audit Quarterly EM&A Summary Report No. 7 for November 2015 to January 2016

(Designated Project Works Area)



| REVISION SCHEDULE | | | | | |
|-------------------|-------------|---|---|---|---|
| Rev | Date | Details | Prepared by | Reviewed by | Approved by |
| 0 | 17 Mar 2016 | Quarterly EM&A Report No. 7 – November 2015 to January 2016 | Adam Zhu | Rodney Ip | YT Tang |
| Signature | | |  |  |  |

| REVISION RECORD | | | | | |
|-----------------|-------------|---|-------------|-------------|-------------|
| Rev | Date | Details | Prepared by | Reviewed by | Approved by |
| 0 | 17 Mar 2016 | Quarterly EM&A Report No. 7 – November 2015 to January 2016 | Adam Zhu | Rodney Ip | YT Tang |

AECOM Consulting Services Limited
 38th Floor, Metroplaza Tower 1
 223 Hing Fong Road
 Kwai Fong, Hong Kong

This document has been prepared in accordance with the scope of the appointment of AECOM Consulting Services Ltd (“ACSL”) with its client and is subject to the terms of that appointment. It is addressed to and for the sole and confidential use and reliance of ACSL’s client. ACSL accepts no liability for any use of this document other than by its client and only for the purposes for which it was prepared and provided. No person other than the client may copy (in whole or in part) use or rely on the contents of this document, without the prior written permission of ACSL (including, without limitation, in the form of a reliance letter) herein or in a separate document. Any advice, opinions, or recommendations within this document should be read and relied upon only in the context of the document as a whole. The contents of this document do not provide legal or tax advice or opinion.

© 2015 AECOM Consulting Services Ltd

TABLE OF CONTENTS

| | |
|---|-----------|
| EXECUTIVE SUMMARY | 1 |
| 1. BASIC PROJECT INFORMATION | 3 |
| 1.1. Introduction | 3 |
| 1.2. Project Organization and Management | 4 |
| 2. SUMMARY OF EM&A REQUIREMENTS | 5 |
| 2.1. Environmental Requirements | 5 |
| 2.2. Environmental Site Inspections | 6 |
| 2.3. Environmental Mitigation Measures | 6 |
| 3. INSPECTION RESULTS | 7 |
| 3.1. Summary of Site Inspections | 7 |
| 3.2. Implementation Status of Environmental Mitigation Measures | 7 |
| 3.3. Status of Environmental Licensing and Permitting | 8 |
| 3.4. Advice on the Solid and Liquid Waste Management Status | 9 |
| 4. COMMENTS, CONCLUSIONS AND RECOMMENDATIONS | 10 |

LIST OF TABLES

| | |
|-----------|--|
| Table 3-1 | Environmental Mitigation Measures |
| Table 3-2 | Summary of Environmental Licensing and Permit Status |
| Table 3-3 | Summary of Quantities of Waste for Reuse or Disposal in this Quarter |

LIST OF FIGURE

| | |
|----------|--------------------------|
| Figure 1 | Organization Chart of ET |
|----------|--------------------------|

LIST OF APPENDICES

| | |
|--------------|---|
| APPENDIX 1 – | SITE LAYOUT PLANS |
| APPENDIX 2 – | CONSTRUCTION PROGRAMME |
| APPENDIX 3 – | THE CONTACT DETAILS OF KEY PERSONNEL OF THE PROJECT |
| APPENDIX 4 – | IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES |

ABBREVIATION

| | |
|------|--|
| CEDD | Civil Engineering and Development Department |
| C&D | Construction & Demolition |
| CNP | Construction Noise Permit |
| EM&A | Environmental Monitoring and Audit |
| EMP | Environmental Management Plan |
| EPD | Environmental Protection Department |
| ET | Environmental Team |
| IEC | Independent Environmental Checker |
| NSR | Noise Sensitive Receiver |
| NT | New Territories |
| PME | Powered Mechanical Equipment |
| RE | Resident Engineer |
| TTS# | Trip-ticket System |

EXECUTIVE SUMMARY

The Environmental Team (ET) of AECOM Consulting Services Limited (former URS Hong Kong Ltd) is appointed by Civil Engineering and Development Department to undertake the Environmental Monitoring and Audit (EM&A) programme for the Contract No. YL/2013/01 entitled “Cycle Tracks from Tuen Mun to Sheung Shui” (the Project). The Project is regulated under the Environmental Permit no. EP-450/2013 (EP).

This Quarterly EM&A report contains the results and findings of site inspection activities and EM&A works carried out by the Works Contractor as required in the contract from November 2015 to January 2016.

Construction Progress

The construction works of the Project was commenced in 28 April 2014. The major construction works in this quarter were listed below:

| Reporting Month | Construction Works |
|------------------------|---|
| November 2015 | Backfilling of retaining wall, installation of bicycle parapet, backfilling and construction of cycle track, drainage, fill slope, resting station and retaining wall |
| December 2015 | Backfilling of retaining wall, installation of bicycle parapet and construction of retaining wall, cycle track, drainage, fill slope and resting station |
| January 2016 | Backfilling of retaining wall, installation of bicycle parapet and construction of cycle track, drainage, fill slope and resting station |

Environmental Issues

Several environmental issues have been identified by the ET during reporting period as listed below:

- Marks of chemical leakage are noted;
- Materials were disposed over the site;
- Excessive accumulation of waste was noted;
- Chemical waste were not labeled and packaged properly;
- Stagnant water was noted;
- Stockpile spread outside the site;

- Broken tree branches were found on site;
- Waste were found at U-shaped channel;
- Materials stored near the river;
- Water should be sprayed where there is dusty activities;
- Chemical leakage from machine;
- Muddy vehicle wheel tracks were found at the entrance and the public road at the site;
- Stockpiles and dust spread outside the site;
- Waste were found at U-shaped channel;
- No drip tray provided for chemical containers;
- Waste were not disposed regularly;
- Materials and stockpile were stocked next to tree

Environmental Monitoring and Audit Progress

According to the “Construction of Cycle tracks and the Associated Supporting Facilities from Sha Po Tsuen to Shek Sheung River Stage 1 Environmental Review EM&A Manual (2013) (EM&A Manual 2013), no air, water and noise monitoring is required.

As no noise monitoring was specified from the EM&A Manual 2013, setting up of Action / Limit Levels is not required.

According to the weekly site inspections carried out in this quarter, it indicated that the Contractor has implemented mitigation measures to address the environmental problems. The measures taken by the Contractor were considered as adequate and effective to minimize negative impact to the environment. On-going investigations will be carried out to observe performance and effectiveness of those measures.

Environmental Complaints, Notices, Summons and Remedial Action

No complaints, summons and notifications were received in this quarter.

1. BASIC PROJECT INFORMATION

1.1. Introduction

1.1.1. AECOM Consulting Services Limited (former URS Hong Kong Ltd) has been commissioned by CEDD as ET for the construction works of ‘Contract No. YL/2013/01 Cycle Track from Tuen Mun to Sheung Shui – Stage 1’ (the Project). The Project commenced in November 2013 and is scheduled for completion by the end of 2016. The construction works of the Project was commenced in 28 April 2014.

1.1.2. The site layout plans and the construction programme are shown in **Appendix 1** and **Appendix 2** respectively.

1.1.3. The Project comprises the following primary works elements:

- Construction of a new cycle track (with footpath) section from near Yuen Long Sha Po Tsuen connecting to the end of the existing cycle track, along Castle Peak Road – Tam Mi Section and along Pok Wai South Road (namely “Section 1”);
- Construction of a new cycle track (with footpath) section from near Ho Sheung Heung along Sheung Yue River and Shek Sheung River connecting to the existing cycle track in Sheung Shui (“namely “Section 1b”);
- Construction of the associated support facilities including two Resting Stations - R5 and R9 integrated with Information Kiosk;
- The associated streetscape, landscape, utilities diversions, traffic aids installation, street lighting, water, sewerage and drainage works; and
- Provision of environmental mitigation measures.

1.1.4. The major construction works in this quarter were listed below:

| Reporting Month | Construction Works |
|-----------------|---|
| November 2015 | Backfilling of retaining wall, installation of bicycle parapet, backfilling and construction of cycle track, drainage, fill slope, resting station and retaining wall |
| December 2015 | Backfilling of retaining wall, installation of bicycle parapet and construction of retaining wall, cycle track, drainage, fill slope and resting station |
| January 2016 | Backfilling of retaining wall, installation of bicycle parapet and construction of cycle track, drainage, fill slope and resting station |

1.1.5. The Project is regulated under the Environmental Permit no. EP-450/2013 (EP).

According to the EP, the monitoring and audit programme shall be implemented in accordance with the procedures and requirements as set out in the EIA Report and EM&A Manual (Register No. AEIAR–133/2009) & the “Construction of Cycle tracks and the Associated Supporting Facilities from Sha Po Tsuen to Shek Sheung River Stage 1 Environmental Review EM&A Manual (2013) (EM&A Manual (2013)).

1.1.6. This Quarterly EM&A report is prepared in accordance with Section 12.5 of the EM&A Manual (2013) to summarize the results and findings of site inspection activities and EM&A works carried out by the Works Contractor as required in the contract from November 2015 to January 2016. The report is to be submitted to the ER, the Contractor, IEC and EPD.

1.1.7. The contact persons and telephone numbers of key personnel for enquiries are shown in **Appendix 3**.

1.2. Project Organization and Management

1.2.1. The Project Organization Chart of the ET is shown in **Figure 1**.

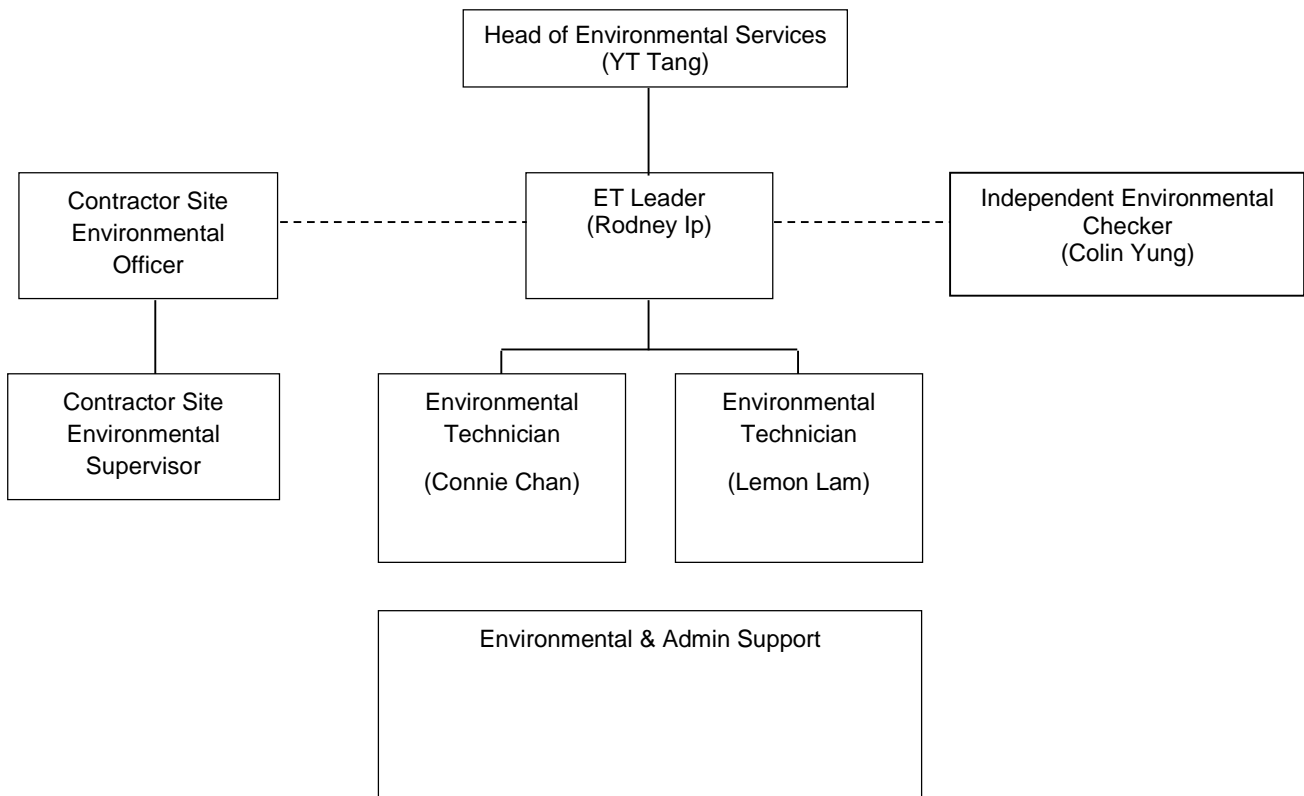


Figure 1 Organization Chart of Environmental Team

2. SUMMARY OF EM&A REQUIREMENTS

2.1. Environmental Requirements

Air Quality

- 2.1.1. The EM&A Manual (2013) identified that no significant impacts could arise during construction and operation of the project. No specific construction dust monitoring was recommended in the EM&A Manual (2013) given proper implementation of the dust control measures under the Air Pollution Control (Construction Dust) Regulation. General air quality control measures are recommended for implementation as good site practice.

Noise

- 2.1.2. The EM&A Manual (2013) identifies that with the use of quiet / silenced PME and noise barriers, where applicable, will result in no unacceptable construction noise. General noise control measures are recommended for implementation as good site practice. No NSR has been identified within 300m of the site working areas and no noise exceedance within the stage 1 designated project works areas were predicted based on the Environmental Review findings, therefore no noise monitoring is recommended under the EM&A Manual (2013). In this connection, setting up of Action / Limit Levels is not required.
- 2.1.3. No construction is planned during restricted hours. If construction is required during restricted hours the Contractor is required to apply for a CNP.

Water Quality

- 2.1.4. The EM&A Manual (2013) identifies that best practicable pollution control measures during construction should be effective to control the potential water quality impacts resulting from stormwater runoff into receiving waters. Water Discharge License has been applied by the Contractor.
- 2.1.5. According to the EM&A Manual (2013), no water quality monitoring is considered necessary within stage 1 designated project works areas based on the Environmental Review findings.

Waste Management

- 2.1.6. The EM&A Manual (2013) identifies that with proper on-site handling and storage (covered containers), reuse (of inert construction wastes) and off-site disposal (via approved waste collectors to approved waste facilities and/or disposal grounds) the generation, handling and disposal of these wastes will not give rise to any adverse environmental impacts. Control and mitigation should be implemented as general good site practices.

Land Contamination

- 2.1.7. The EM&A Manual (2013) considers that no specific EM&A requirements are necessary for Land Contamination.

Ecology and Fisheries

- 2.1.8. The EM&A Manual (2013) identifies that no significant overall loss of valuable ecological habitat and fishponds and it is considered that no significant negative impacts to surrounding habitats and species and aquaculture or water quality will arise from the construction and operation of the cycle track given that appropriate mitigation measures and good practices are properly implemented. No specific ecological or fisheries monitoring is required.

Cultural Heritage

- 2.1.9. The EM&A Manual (2013) identifies that no adverse impacts on cultural heritage resources would be expected from the construction or operational phase of the Project. No specific monitoring is required during the construction phase. However, care has been taken during construction stage to report any signs of possible discovery of artefacts to minimize potential impacts during the construction phase.

Landscape and Visual

- 2.1.10. Based on the EM&A Manual's recommendation, all measures undertaken during the construction stage shall be audited by the Landscape Architect as a member of the Environmental Team. The site inspections were undertaken for twice a month during this reporting period to ensure all the recommended landscape and visual mitigation measures have been effectively implemented.

2.2. Environmental Site Inspections

- 2.2.1. Environmental site inspections are required to inspect the construction activities of the Project in order to ensure that appropriate environmental protection and pollution control mitigation measures are properly implemented. Regular site inspections should be carried out once per week during the construction phase.

2.3. Environmental Mitigation Measures

- 2.3.1. Required environmental mitigation measures shall be implemented according to the approved EM&A Manual (2013) as subject to the site condition.
- 2.3.2. The environmental mitigation measures that recommended in the Implementation Schedule in the EM&A Manual (2013) are presented in **Appendix 4**.

3. INSPECTION RESULTS

3.1. Summary of Site Inspections

3.1.1. According to the summary of the weekly site inspections carried out in this quarter, it indicated that the environmental condition has no contrast with the EIA predictions after implementing proper environmental mitigation measures.

3.2. Implementation Status of Environmental Mitigation Measures

3.2.1. According to the weekly site inspections carried out in this quarter, it indicated that the Contractor has implemented mitigation measures to address the environmental problems. The measures taken by the Contractor were considered as adequate and effective to minimize negative impact to the environment. On-going investigations will be carried out to observe performance and effectiveness of those measures.

3.2.2. Environmental mitigation measures generally implemented in this reporting period are summarized in **Table 3-1**.

Table 3-1 Environmental Mitigation Measures

| Issues | Environmental Mitigation Measures |
|-------------------------------|--|
| Water Quality | <ul style="list-style-type: none"> • Relocated the stockpile and dusty materials from the river • Remove of stagnant water • Removed or covered the stockpile and dusty materials properly |
| Air Quality | <ul style="list-style-type: none"> • Removed or covered the exposed stockpile and dusty materials • Sprayed water during dry weather to minimize dust condition |
| Noise | <ul style="list-style-type: none"> • Temporary noise barriers installed at works area as needed • Noise baffles/screens to noisy machines/site activities as necessary |
| Waste and Chemical Management | <ul style="list-style-type: none"> • Removed the machines with chemical leakage from the site • Removed the empty chemical containers and materials disposed at U-shaped channel • Removed the broken branches from site • Dispose of wastes regularly |
| General | <ul style="list-style-type: none"> • Relocated/removed the material and stockpile from trees • C&D materials were stored in designated area properly • The tree is maintained and protected properly |

3.3. Status of Environmental Licensing and Permitting

3.3.1. The status of licenses and permits is summarized in **Table 3-2**.

Table 3-2 Summary of Environmental Licensing and Permit Status

| Item No. | Description | Application Date | Date of Issue | Ref. No | Date of Expiry |
|----------|--|------------------|---------------|--------------------------|----------------|
| 1 | Environmental Permit (EP) | N.A | 30 May 2013 | EP-450/2013 | N.A. |
| 2 | Registration as a Chemical Waste Producer | N.A | 10 Jan 2014 | WPN5213-524-S3 777-01 | N.A |
| 3 | Effluent Discharge License | N.A | 25 Feb 2014 | W5/113841/1 | 28 Feb 2019 |
| 4 | Account for Disposal of Construction Waste | N.A. | 16 Dec 2013 | 7018953 | N.A. |
| 5 | Construction Noise Permit | As required | N.A. | N.A. | N.A. |

3.3.2. Non-compliance with EP conditions and other requirements associated with the construction of this Contract was not identified in this reporting period.

3.3.3. No environmental complaint and environmental summons were received in this reporting period

3.4. Advice on the Solid and Liquid Waste Management Status

- 3.4.1. The quantities of waste for reuse or disposal in this reporting period are summarized in **Table 3-3**.
- 3.4.2. It is recommended to maximize the reuse or recycle of the C&D material. The Contractor transported the remaining inert C&D material to public fill for disposal and disposed of non-inert wastes such as general refuses and materials segregated to North East New Territory (NENT) Landfill after sorting out the recyclables.

Table 3-3 Summary of Quantities of Waste for Reuse or Disposal in this Quarter

| Type of Waste | | Quantity | Disposal Location | Cumulative Quantity |
|---------------------|--|----------|---|---------------------|
| Inert C&D Materials | Total Quantity Generated (in '000m ³) | 0.17 | TM Area 38 | 4.577 |
| | Hard Rock and Large Broken Concrete (in '000m ³) | 0 | TM Area 38 | 0 |
| | Reused in the Contract (in '000m ³) | 0 | N.A. | 0 |
| | Reused in other Projects (in '000m ³) | 0 | N.A. | 0.62 |
| | Disposed as Public Fill (in '000m ³) | 0.17 | TM Area 38 | 3.957 |
| C&D Waste | Metals (in '000kg) | 0.03 | Recycling Facilities | 0.172 |
| | Paper/cardboard packing (in '000kg) | 0.03 | Recycling Facilities | 0.192 |
| | Plastic (in '000kg) | 0.03 | Recycling Facilities | 0.192 |
| | Chemical Waste (in '000kg) | 0 | Chemical Waste Treatment Centre (CWTC) | 0.02 |
| | Others, e.g. general refuse (in '000m ³) | 0.28 | NENT / public waste collection facilities | 0.818 |

- 3.4.3. The Contractor should provide sufficient waste storage facilities on site such as rubbish bins and fenced-off waste storage areas. Waste should be regularly removed from around the site.
- 3.4.4. The Contractor was reminded to increase the frequency of inspection to pump accumulated water from stagnant water ponds when necessary.

4. COMMENTS, CONCLUSIONS AND RECOMMENDATIONS

- 4.1.1. In this quarter, major site activities were backfilling of retaining wall, installation of bicycle parapet and backfilling and construction of cycle track, construction of drainage, fill slope, resting station and retaining wall (concreting, formworks, steelworks)
- 4.1.2. No environmental complaints, notification of summons and prosecutions with respect to environmental issues were received in this quarter.
- 4.1.3. According to the weekly site inspections carried out in this quarter, it indicated that the Contractor has implemented mitigation measures to address the environmental problems. The measures taken by the Contractor were considered as adequate and effective to minimize negative impact to the environment. Ongoing investigations will be carried out to observe performance and effectiveness of those measures.
- 4.1.4. According to the environmental site inspections performed in this quarter, the following recommendations were provided:

Air Quality

- 4.1.5. Undertake water spraying or utilization of tarpaulins on the stockpiling area; and
- 4.1.6. Wash the vehicle wheels properly before leaving

Water Quality

- 4.1.7. Well enclose the exposed stockpile & dusty materials in storage near the river; and
- 4.1.8. Remove the stagnant water or provide pesticide for the stagnant water in the permanent desilting chambers, if any

Chemical and Waste Management



- 4.1.9. Remove the machines with chemical leakage from the site and clear the leakage marks, if applicable;
- 4.1.10. Fence off waste storage areas;
- 4.1.11. Remove waste materials from the site to avoid accumulation regularly; and
- 4.1.12. Properly store and label the chemicals, drip trays should be provided properly

Ecology

- 4.1.13. Clear/Pump out any stagnant water to prevent spillage and run-off water entering natural streams from works;
- 4.1.14. Do not locate stockpile of construction material or debris close to the tree planting areas; and
- 4.1.15. Maintain proper tree protections




APPENDIX 1

SITE LAYOUT PLANS

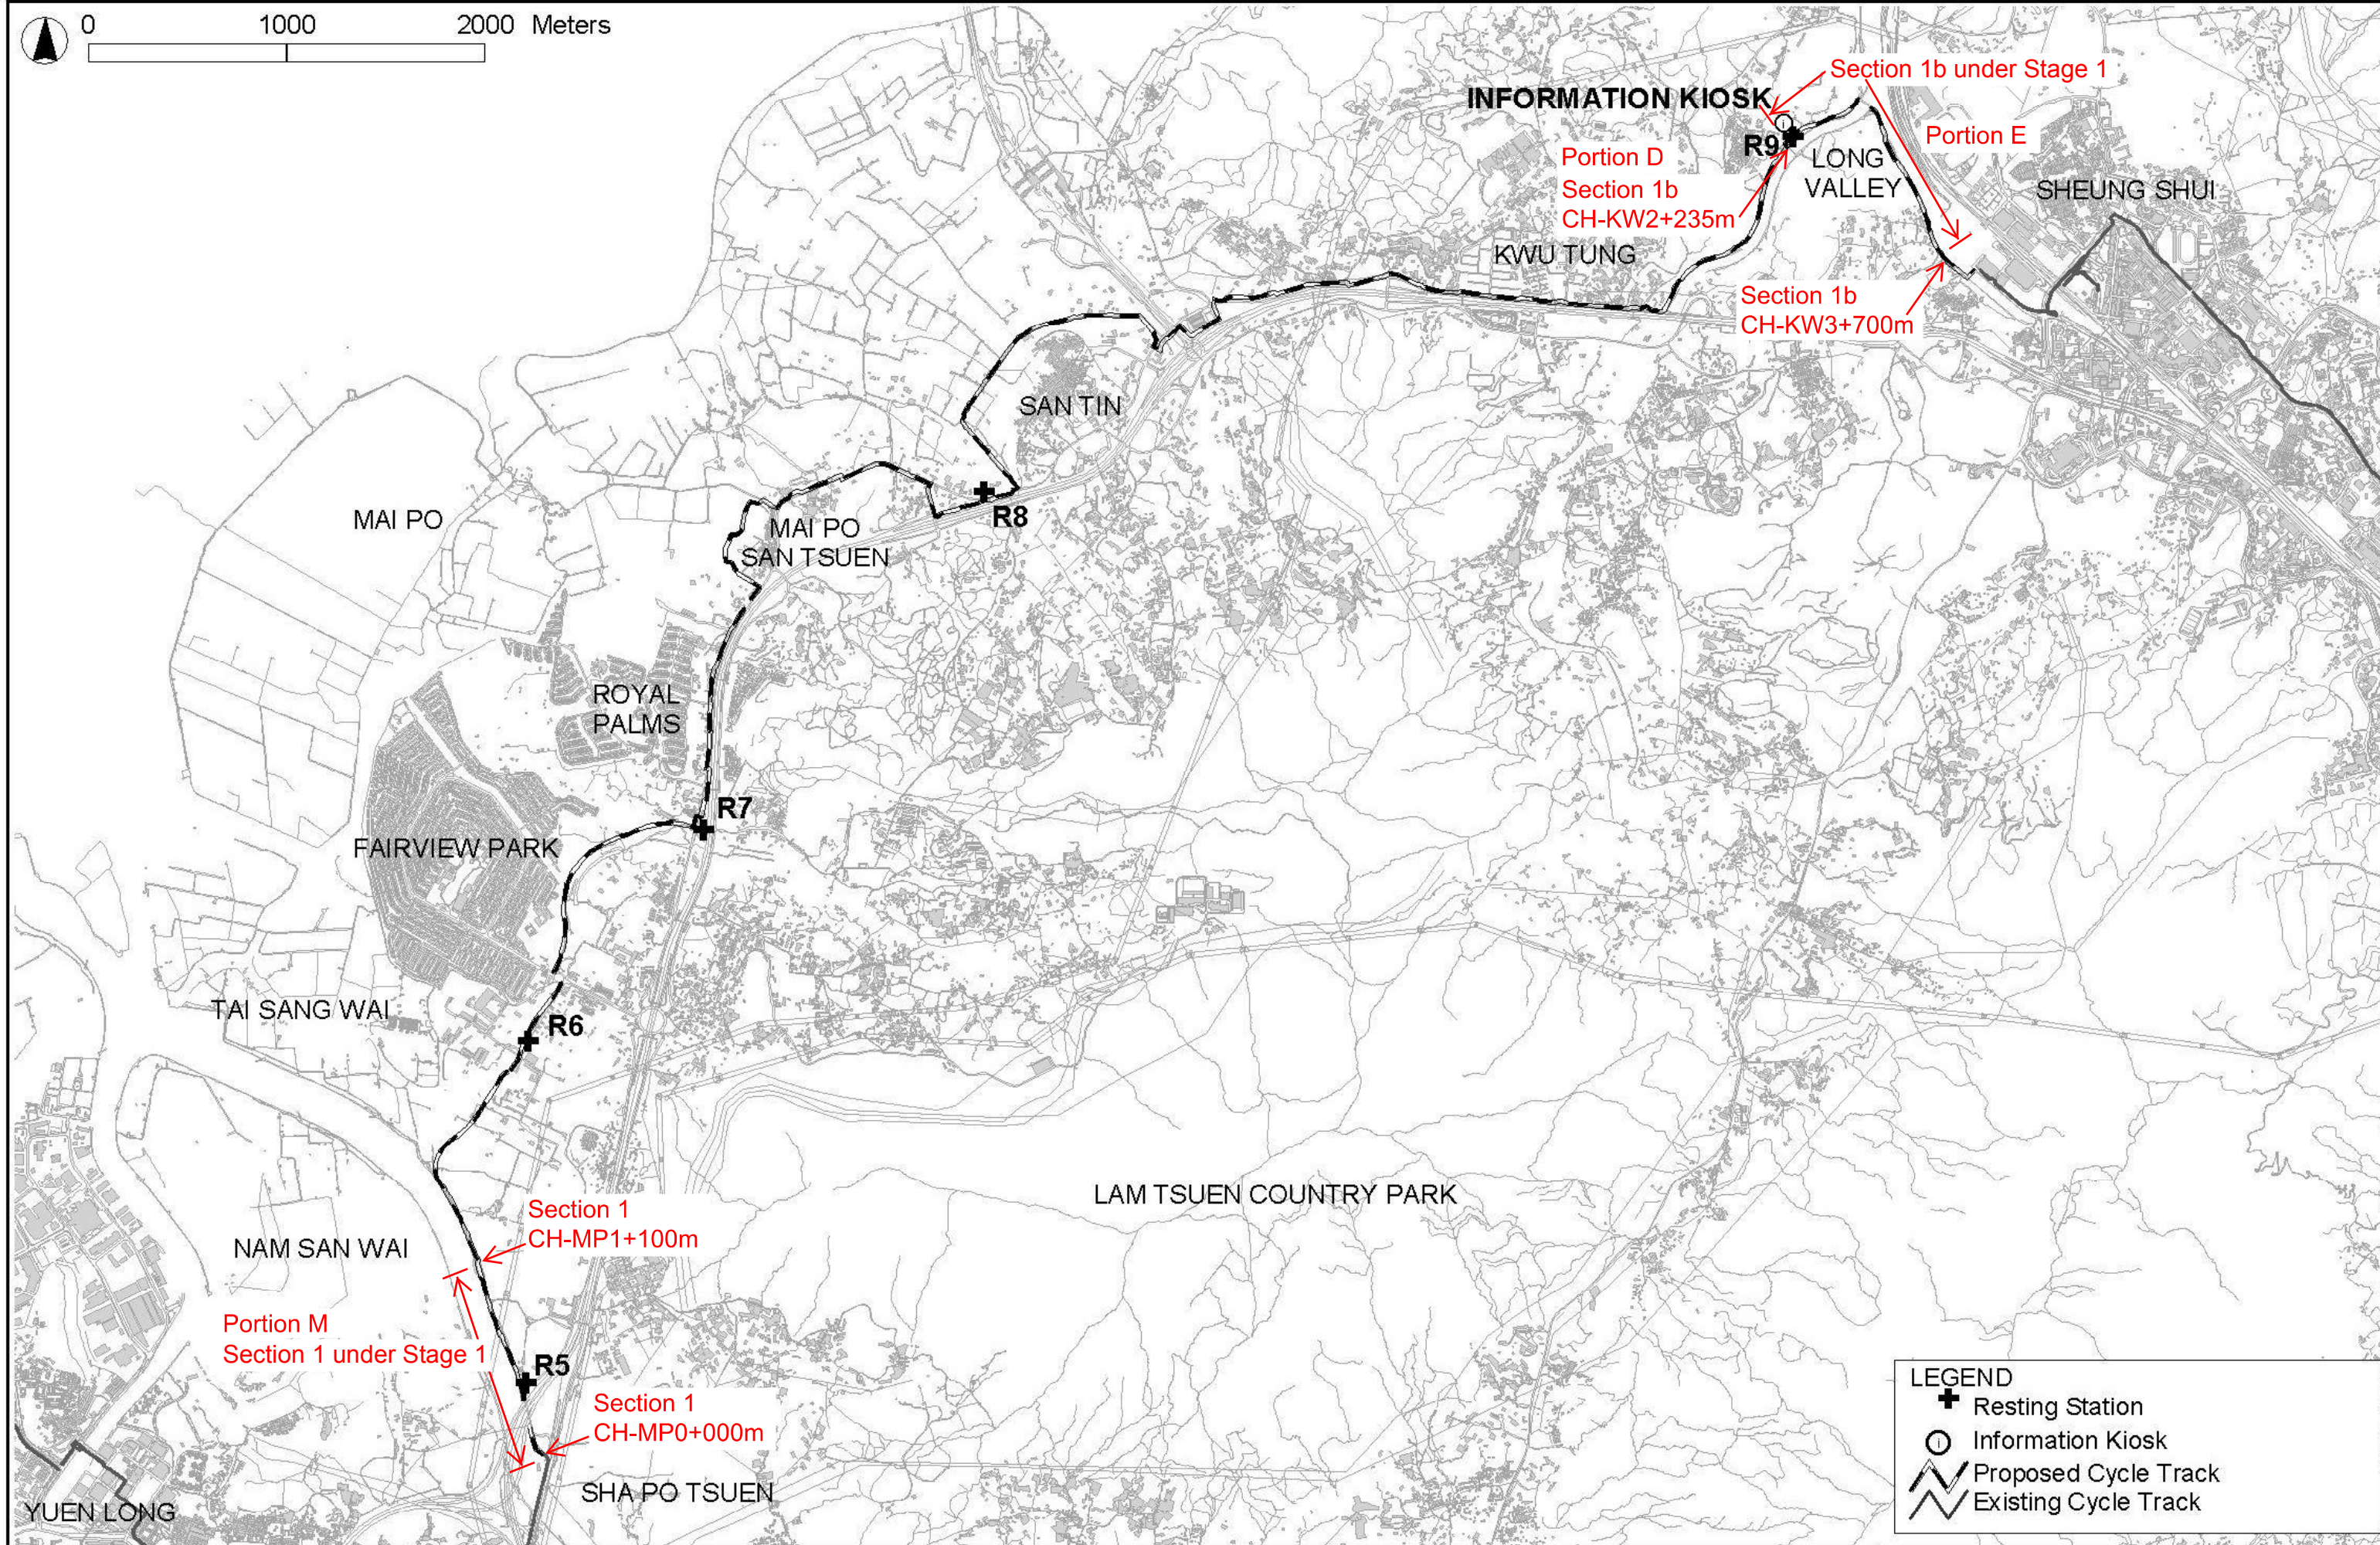

LEGEND

- Resting Station
- Information Kiosk
- Proposed Cycle Track
- Existing Cycle Track

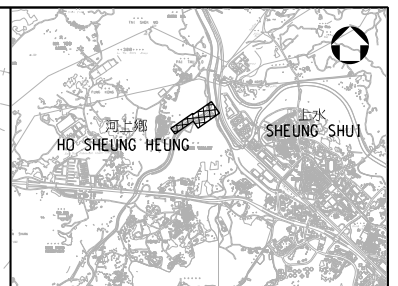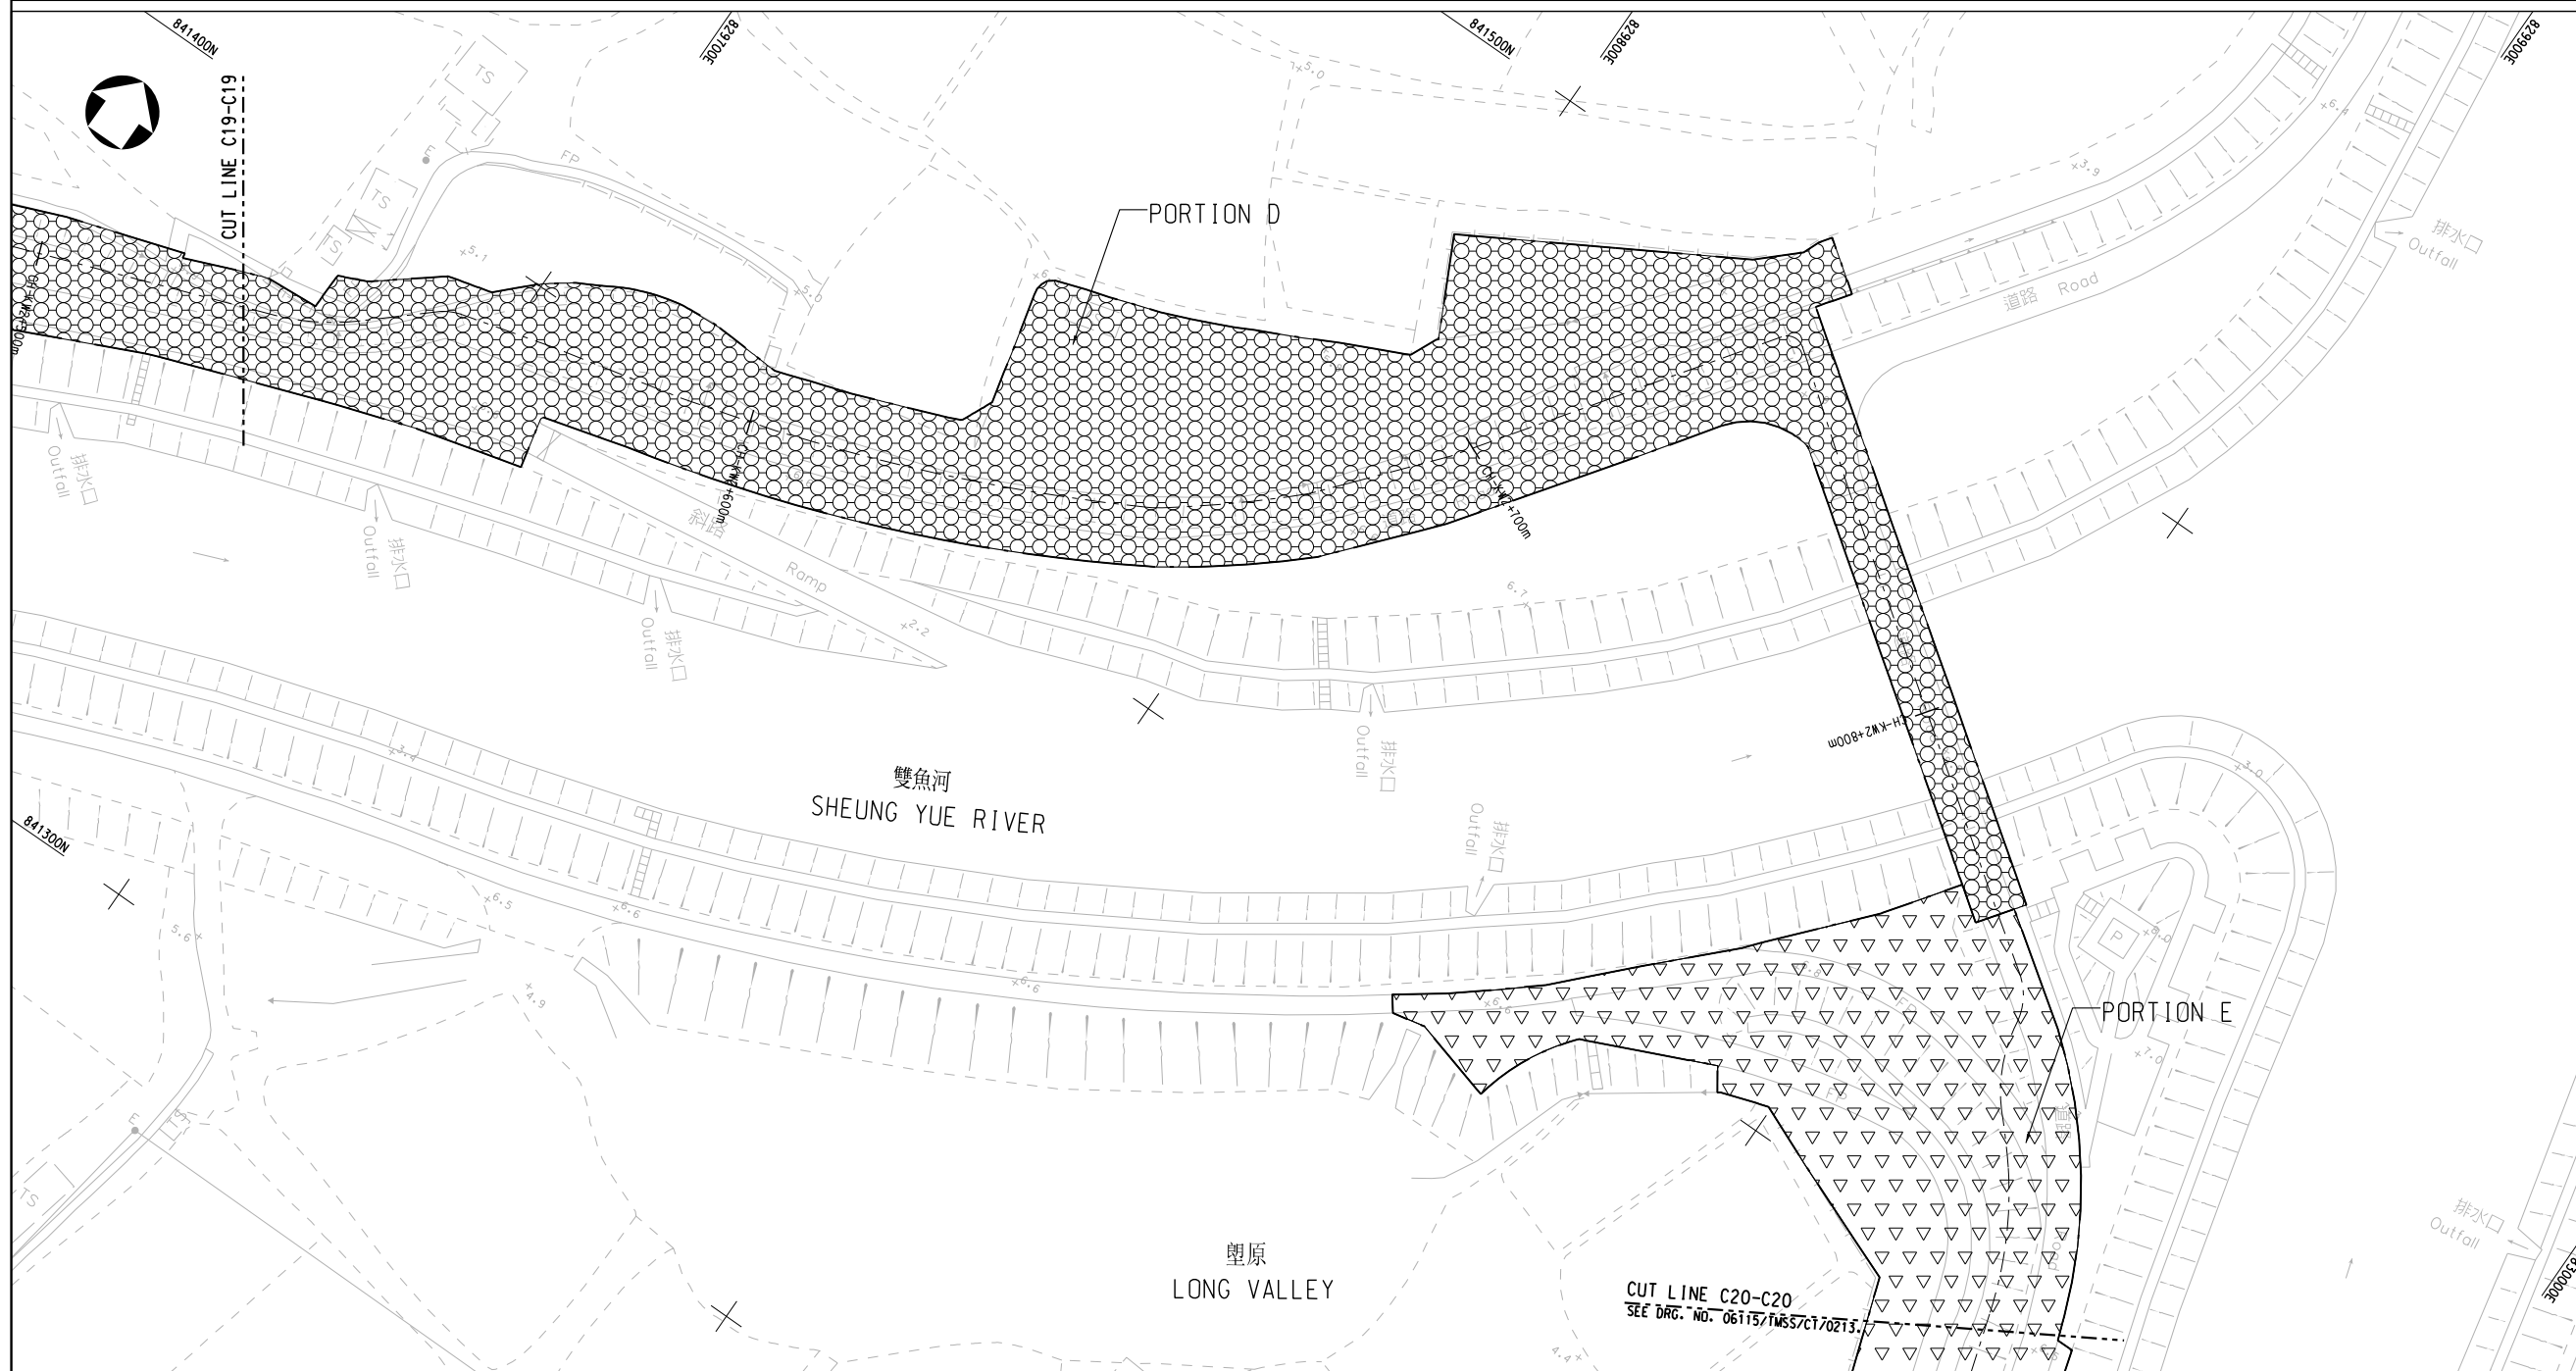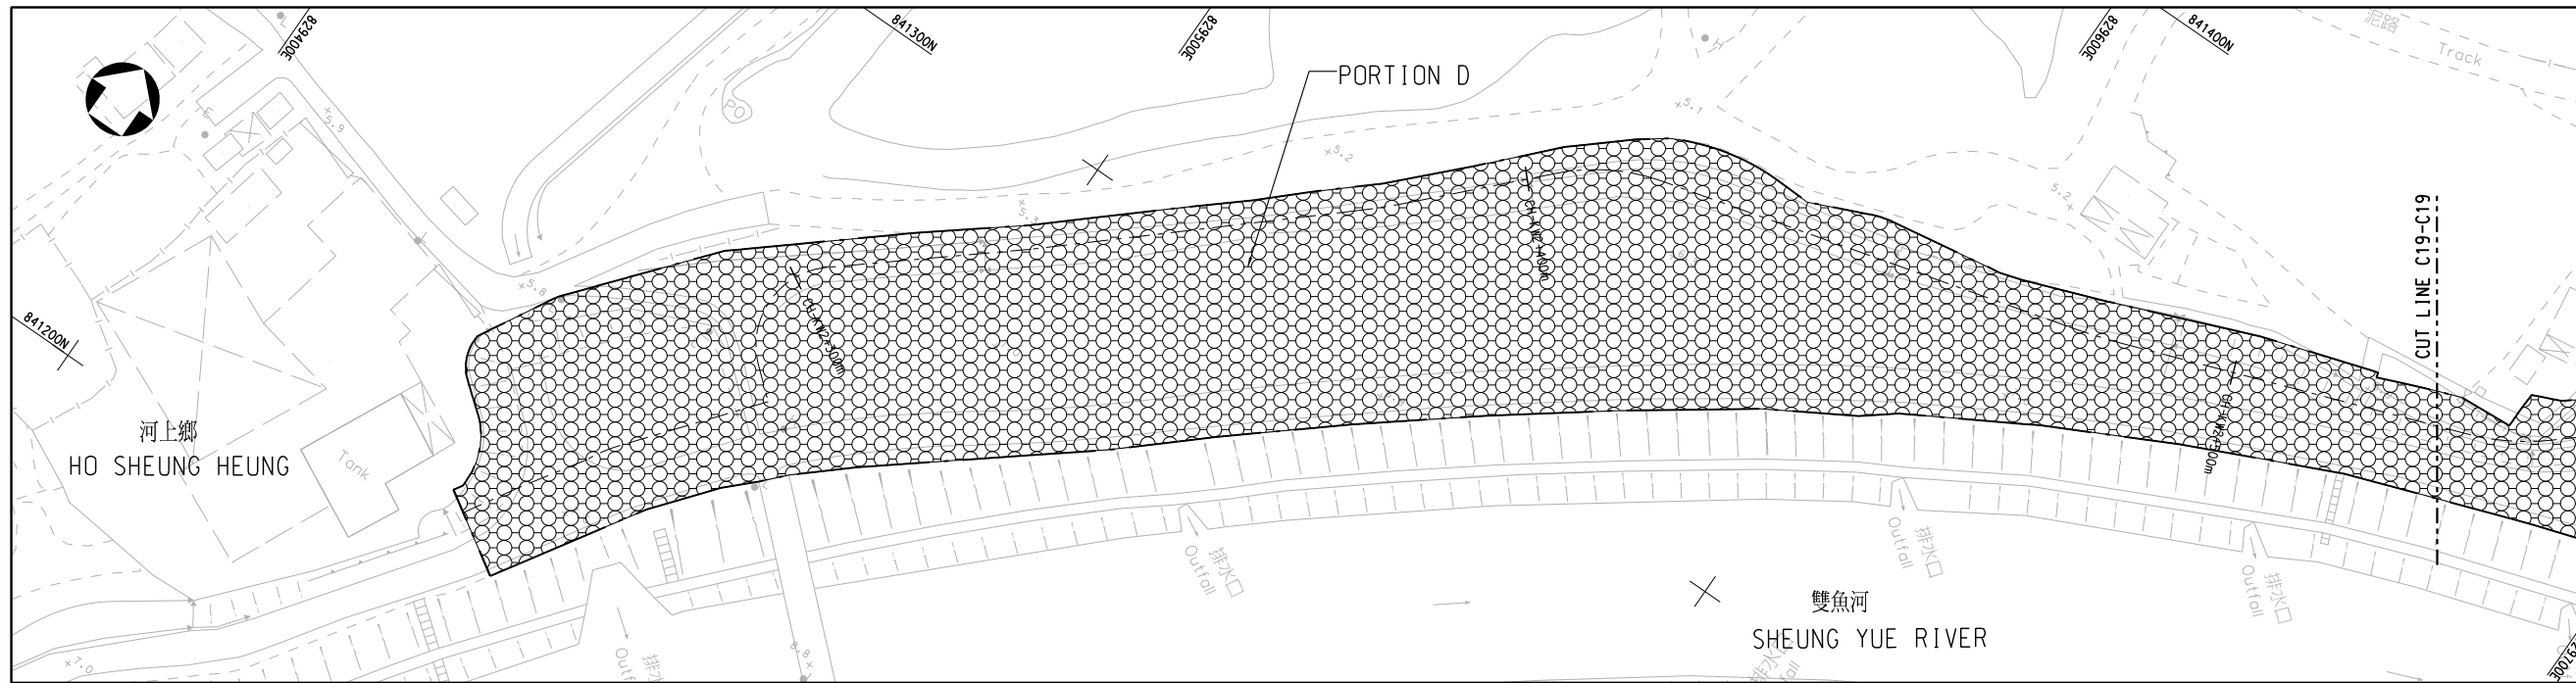

KEY PLAN
N.T.S.

NOTES :
1. FOR NOTES AND LEGEND, REFER TO DRG. NO. 06115/TMSS/CT/0202.

| | | | | |
|---|-------|------------------------|-----|----|
| - | 12/13 | ISSUE FOR CONSTRUCTION | NYH | GT |
|---|-------|------------------------|-----|----|

| Rev. | Date | Description | Drawn | Checked |
|------|------|-------------|-------|---------|
| 修訂 | 日期 | 內容摘要 | 繪圖 | 校核 |



土木工程拓展署
CEDD Civil Engineering and
Development Department

CONTRACT NO. YL/2013/01
CYCLE TRACKS FROM TUEN MUN
TO SHEUNG SHUI - STAGE 1

PORTION OF THE SITE
(SHEET 12 OF 13)

| | | | | |
|---------------------|---------------------|---------------|--------------|-------------------------|
| Drawing No. 圖則編號 | 06115/TMSS/CT/00212 | | | |
| Designed 設計 | Drawn 繪圖 | Checked 校核 | Scale 比例 | 1:500(A1) 1:1000(A3) |
| Approved 批准 | TSN | Date 日期 | Status 狀態 | 12/13 CONSTRUCTION |



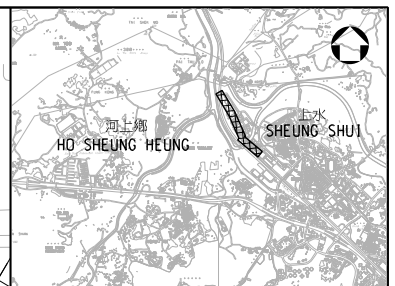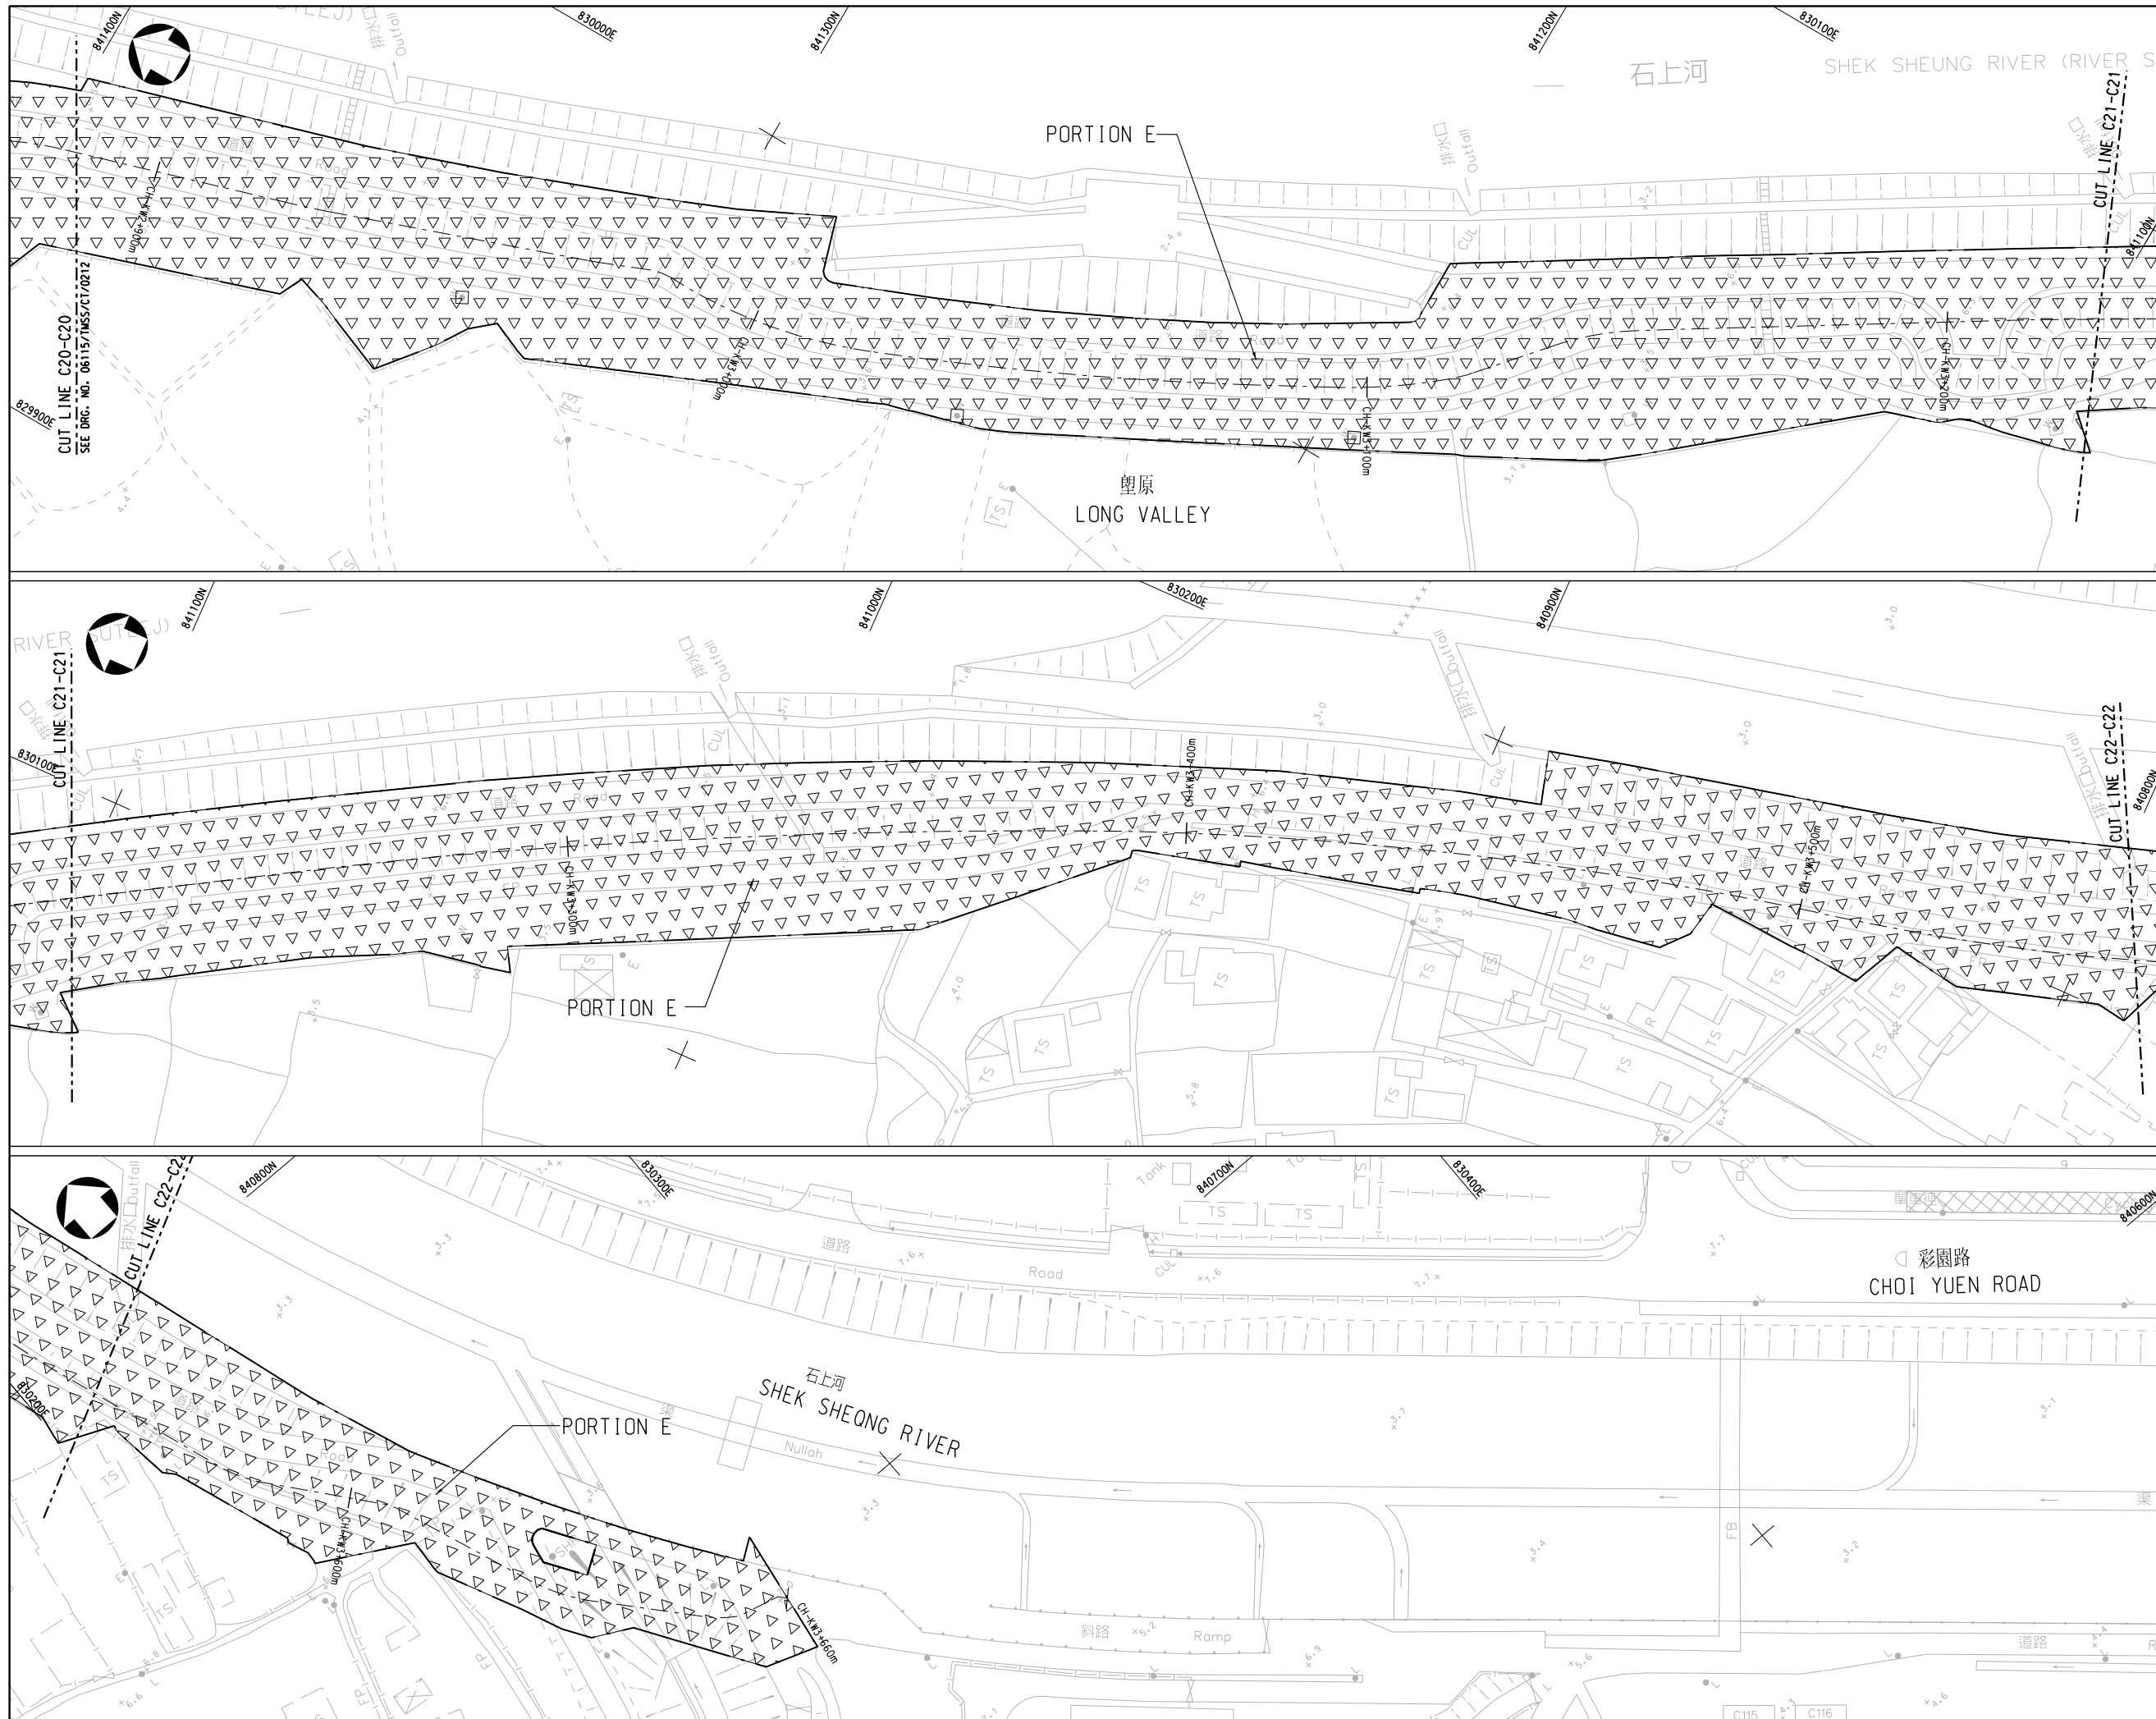

KEY PLAN
N.T.S.

NOTES :
1. FOR NOTES AND LEGEND, REFER TO DRG. NO. 06115/TMSS/CT/0202.

| | | | | |
|-------|------|------------------------|-------|---------|
| Rev. | Date | Description | Drawn | Checked |
| 12/13 | | ISSUE FOR CONSTRUCTION | NYH | GT |




土木工務拓展署
CEDD Civil Engineering and
Development Department

CONTRACT NO. YL/2013/01
CYCLE TRACKS FROM TUEN MUN
TO SHEUNG SHUI - STAGE 1

PORTION OF THE SITE
(SHEET 13 OF 13)

| | | | | |
|-------------|---------------------|--------------|-----------|------------|
| Drawing No. | 06115/TMSS/CT/00213 | | | |
| Designed | Drawn | Checked | Scale | Scale |
| GT | HAX | DCSC | 1:500(A1) | 1:1000(A3) |
| Approved | Date | Status | | |
| TSN | 12/13 | CONSTRUCTION | | |



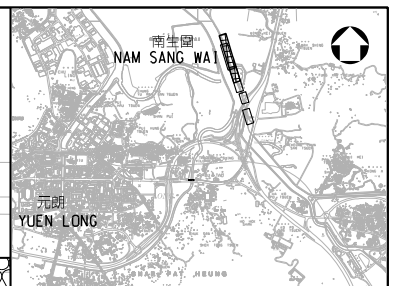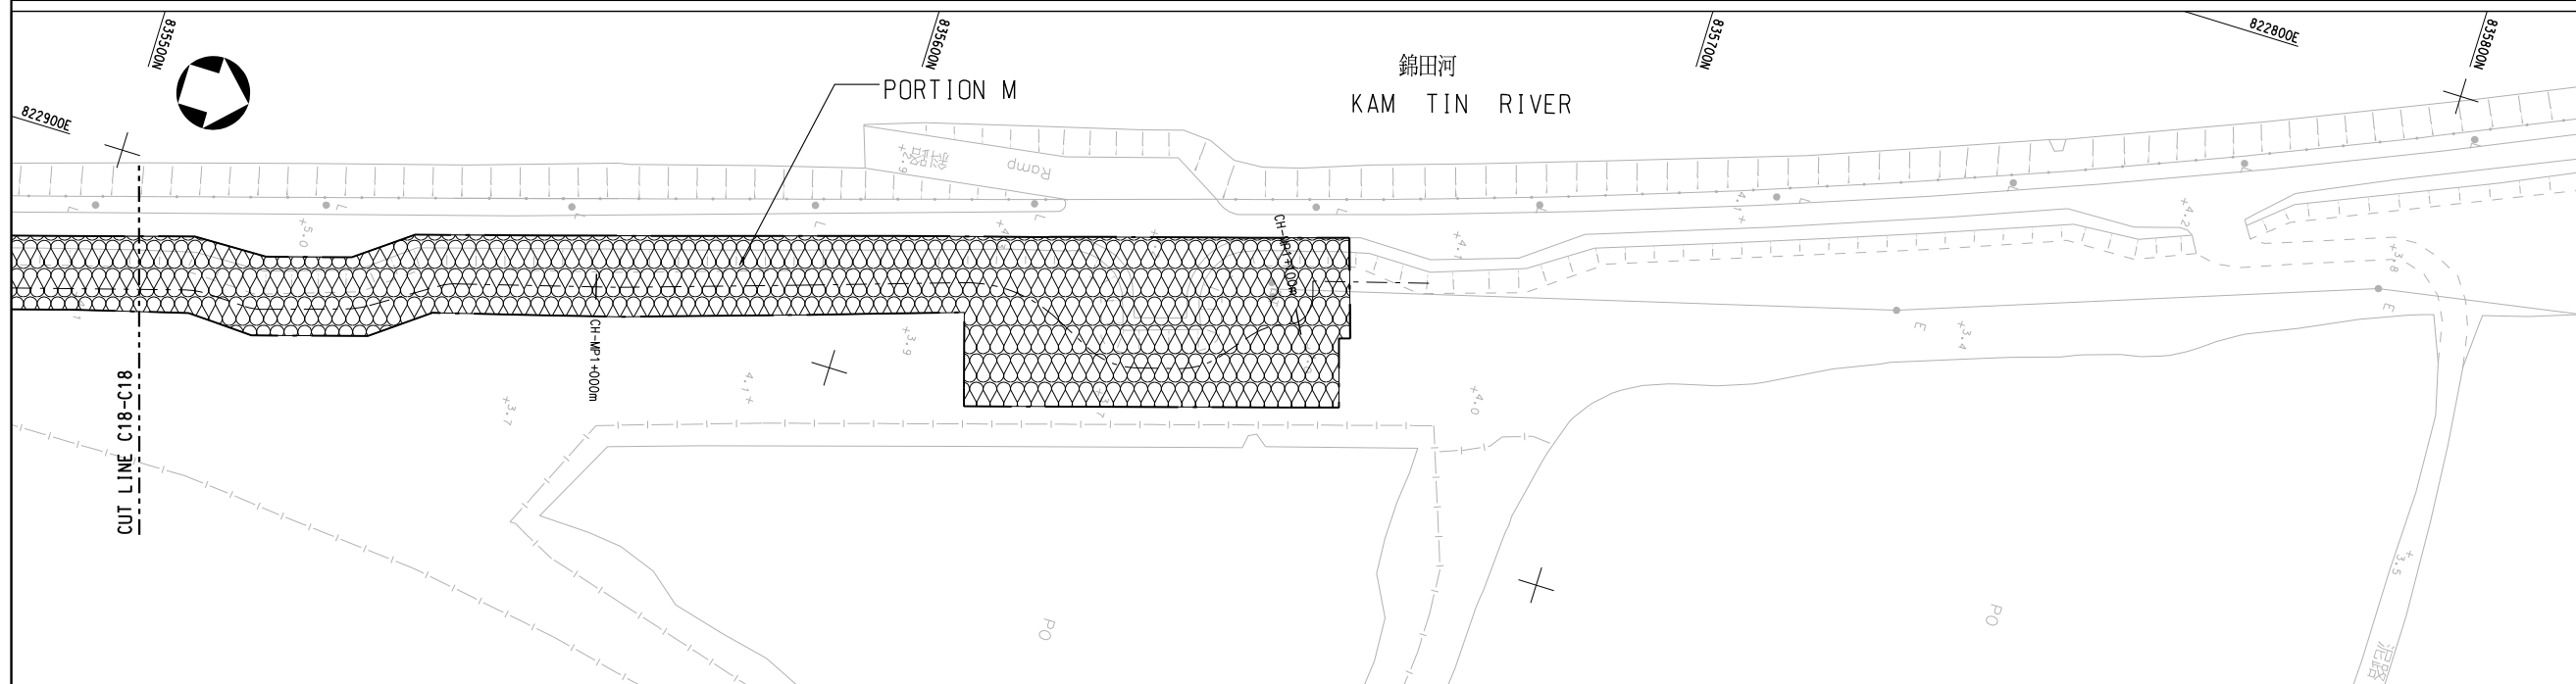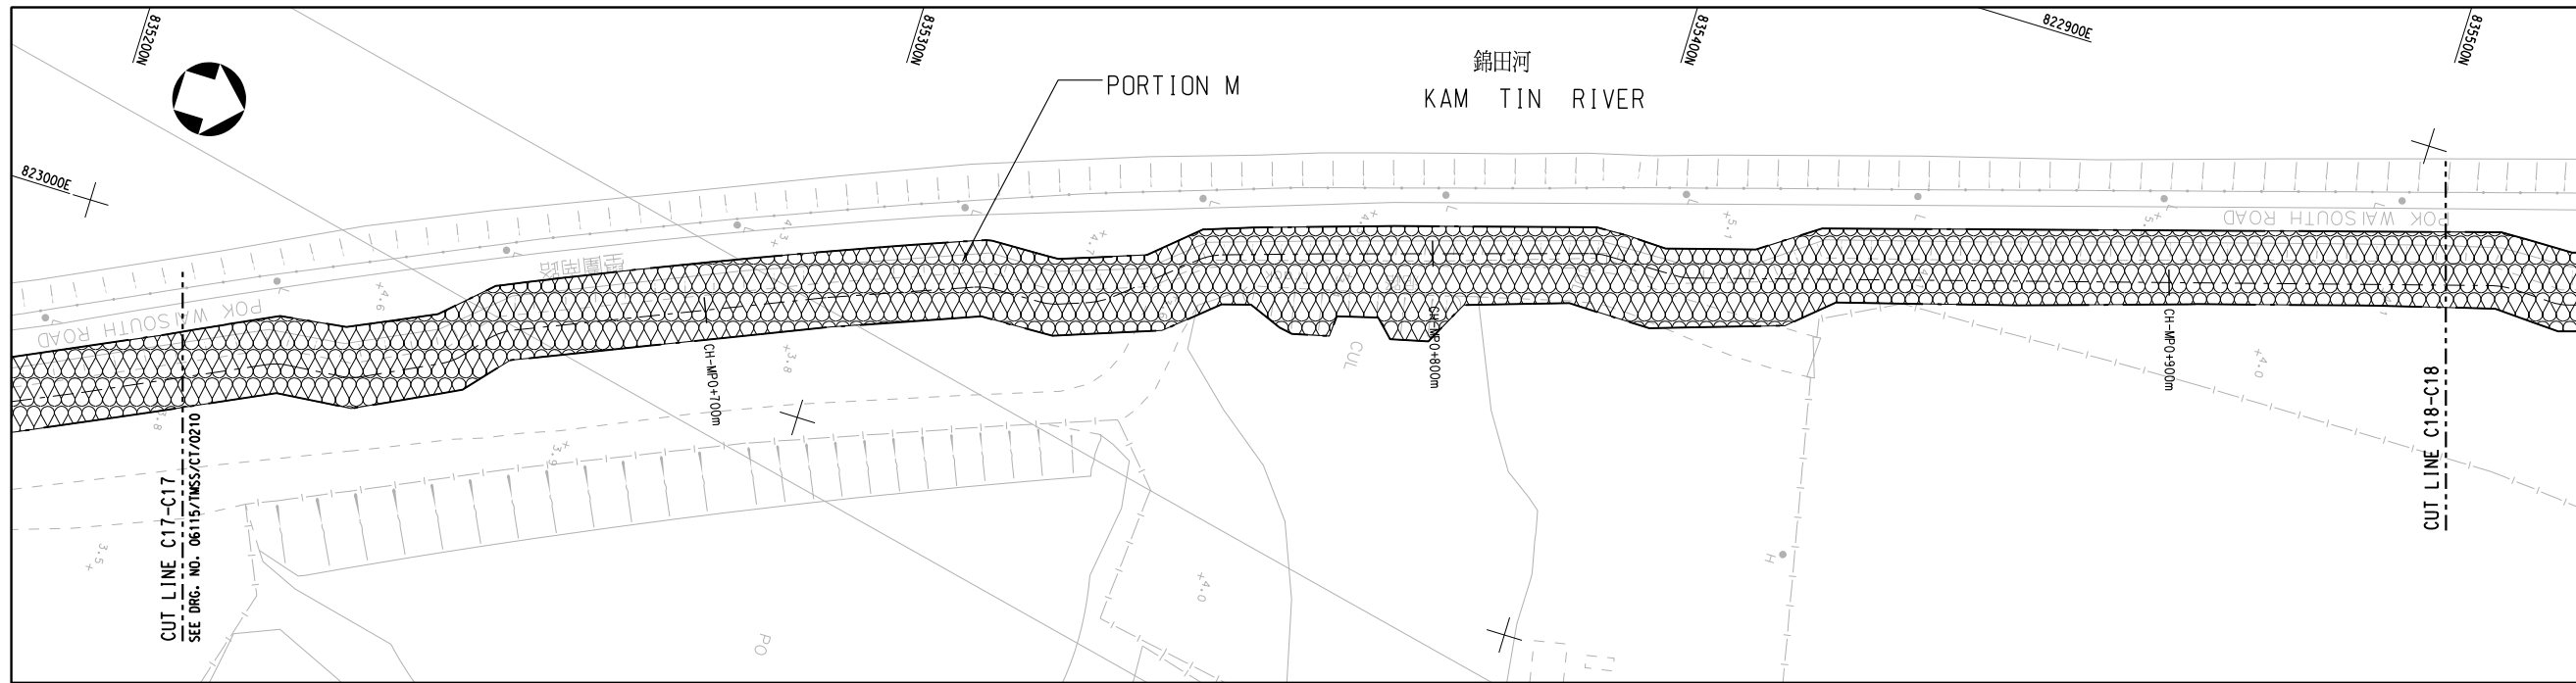

KEY PLAN
N.T.S.

NOTES :
1. FOR NOTES AND LEGEND, REFER TO DRG. NO. 06115/TMSS/CT/0202.

| | | | | |
|------|-------|------------------------|-------|---------|
| Rev. | Date | Description | Drawn | Checked |
| - | 12/13 | ISSUE FOR CONSTRUCTION | NYH | GT |

CEDD 土木工程拓展署
Civil Engineering and
Development Department

CONTRACT NO. YL/2013/01
CYCLE TRACKS FROM TUEN MUN
TO SHEUNG SHUI - STAGE 1

PORTION OF THE SITE
(SHEET 11 OF 13)

| | | | | |
|------------|---------------------|--------------|------------|--|
| Design No. | 06115/TMSS/CT/00211 | | | |
| Designed | Drawn | Checked | Scale | |
| GT | HAX | DCSC | 1:500(A1) | |
| Approved | Date | Status | 比例 | |
| TSN | 12/13 | CONSTRUCTION | 1:1000(A3) | |




APPENDIX 2


CONSTRUCTION PROGRAMME

Cycle Tracks from Tuen Mun to Sheugn Shui - Stage 1

Project Programme of the Works

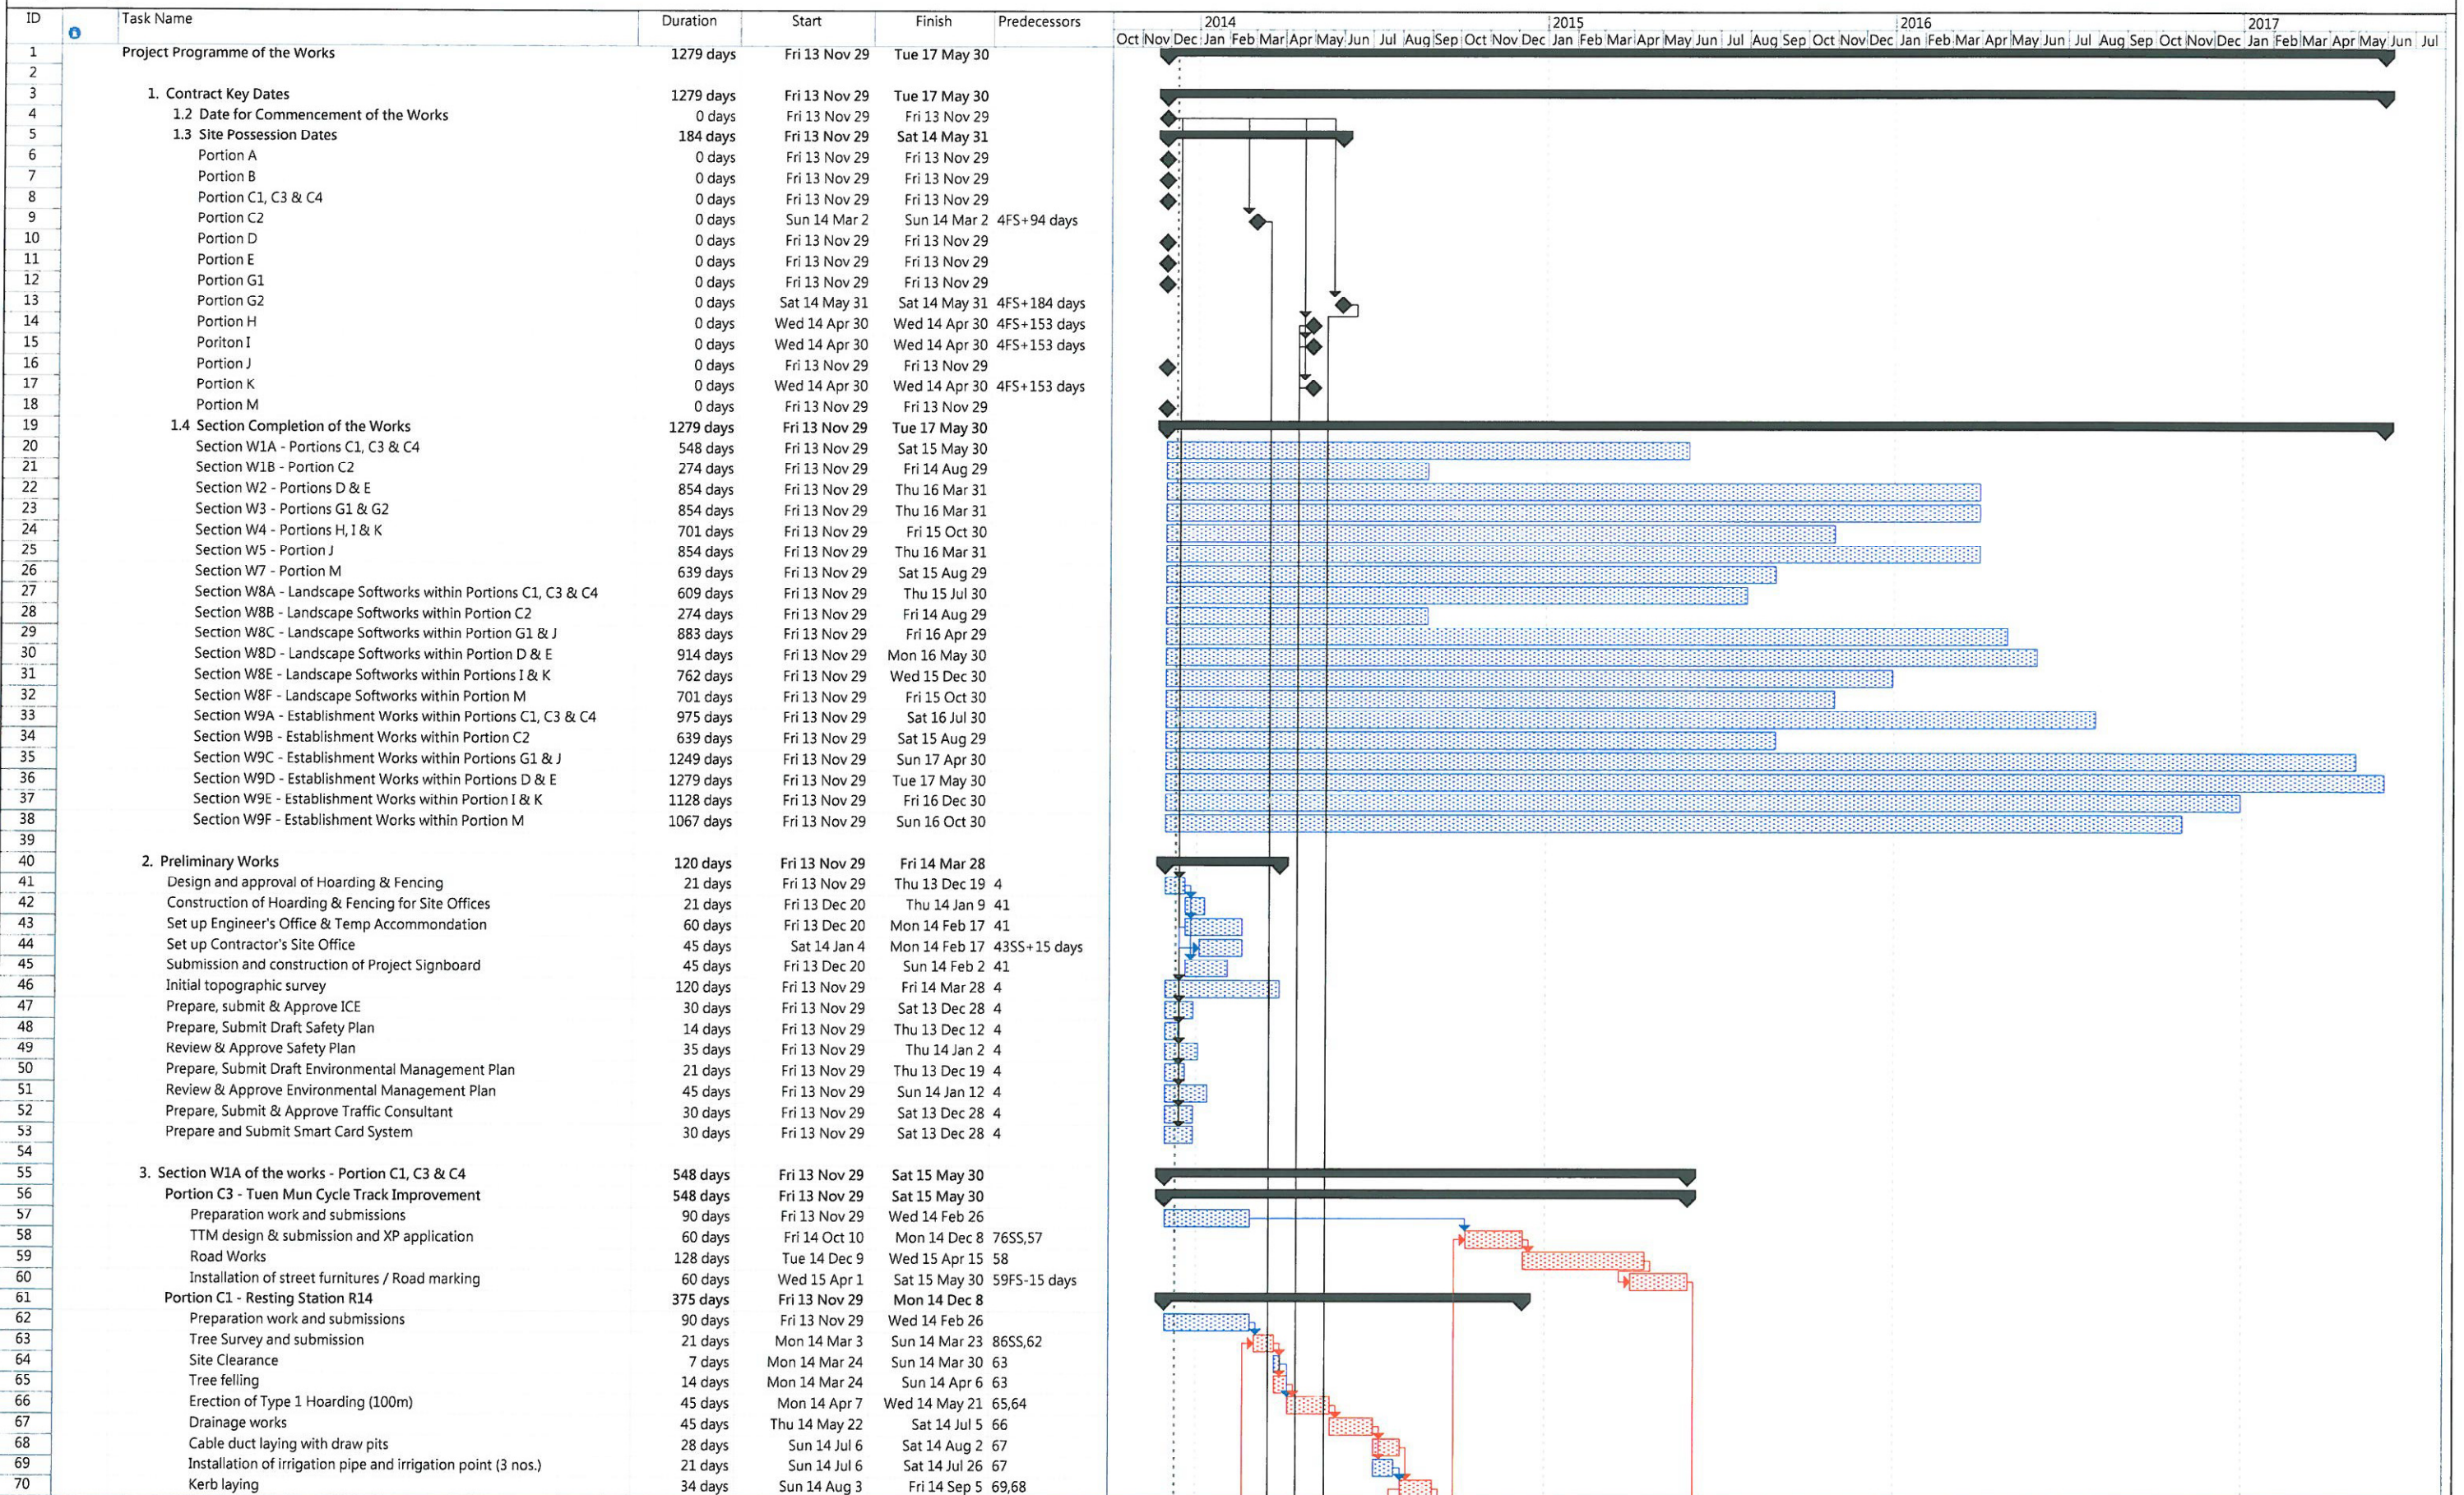


Cycle Tracks from Tuen Mun to Sheugn Shui - Stage 1
Project Programme of the Works

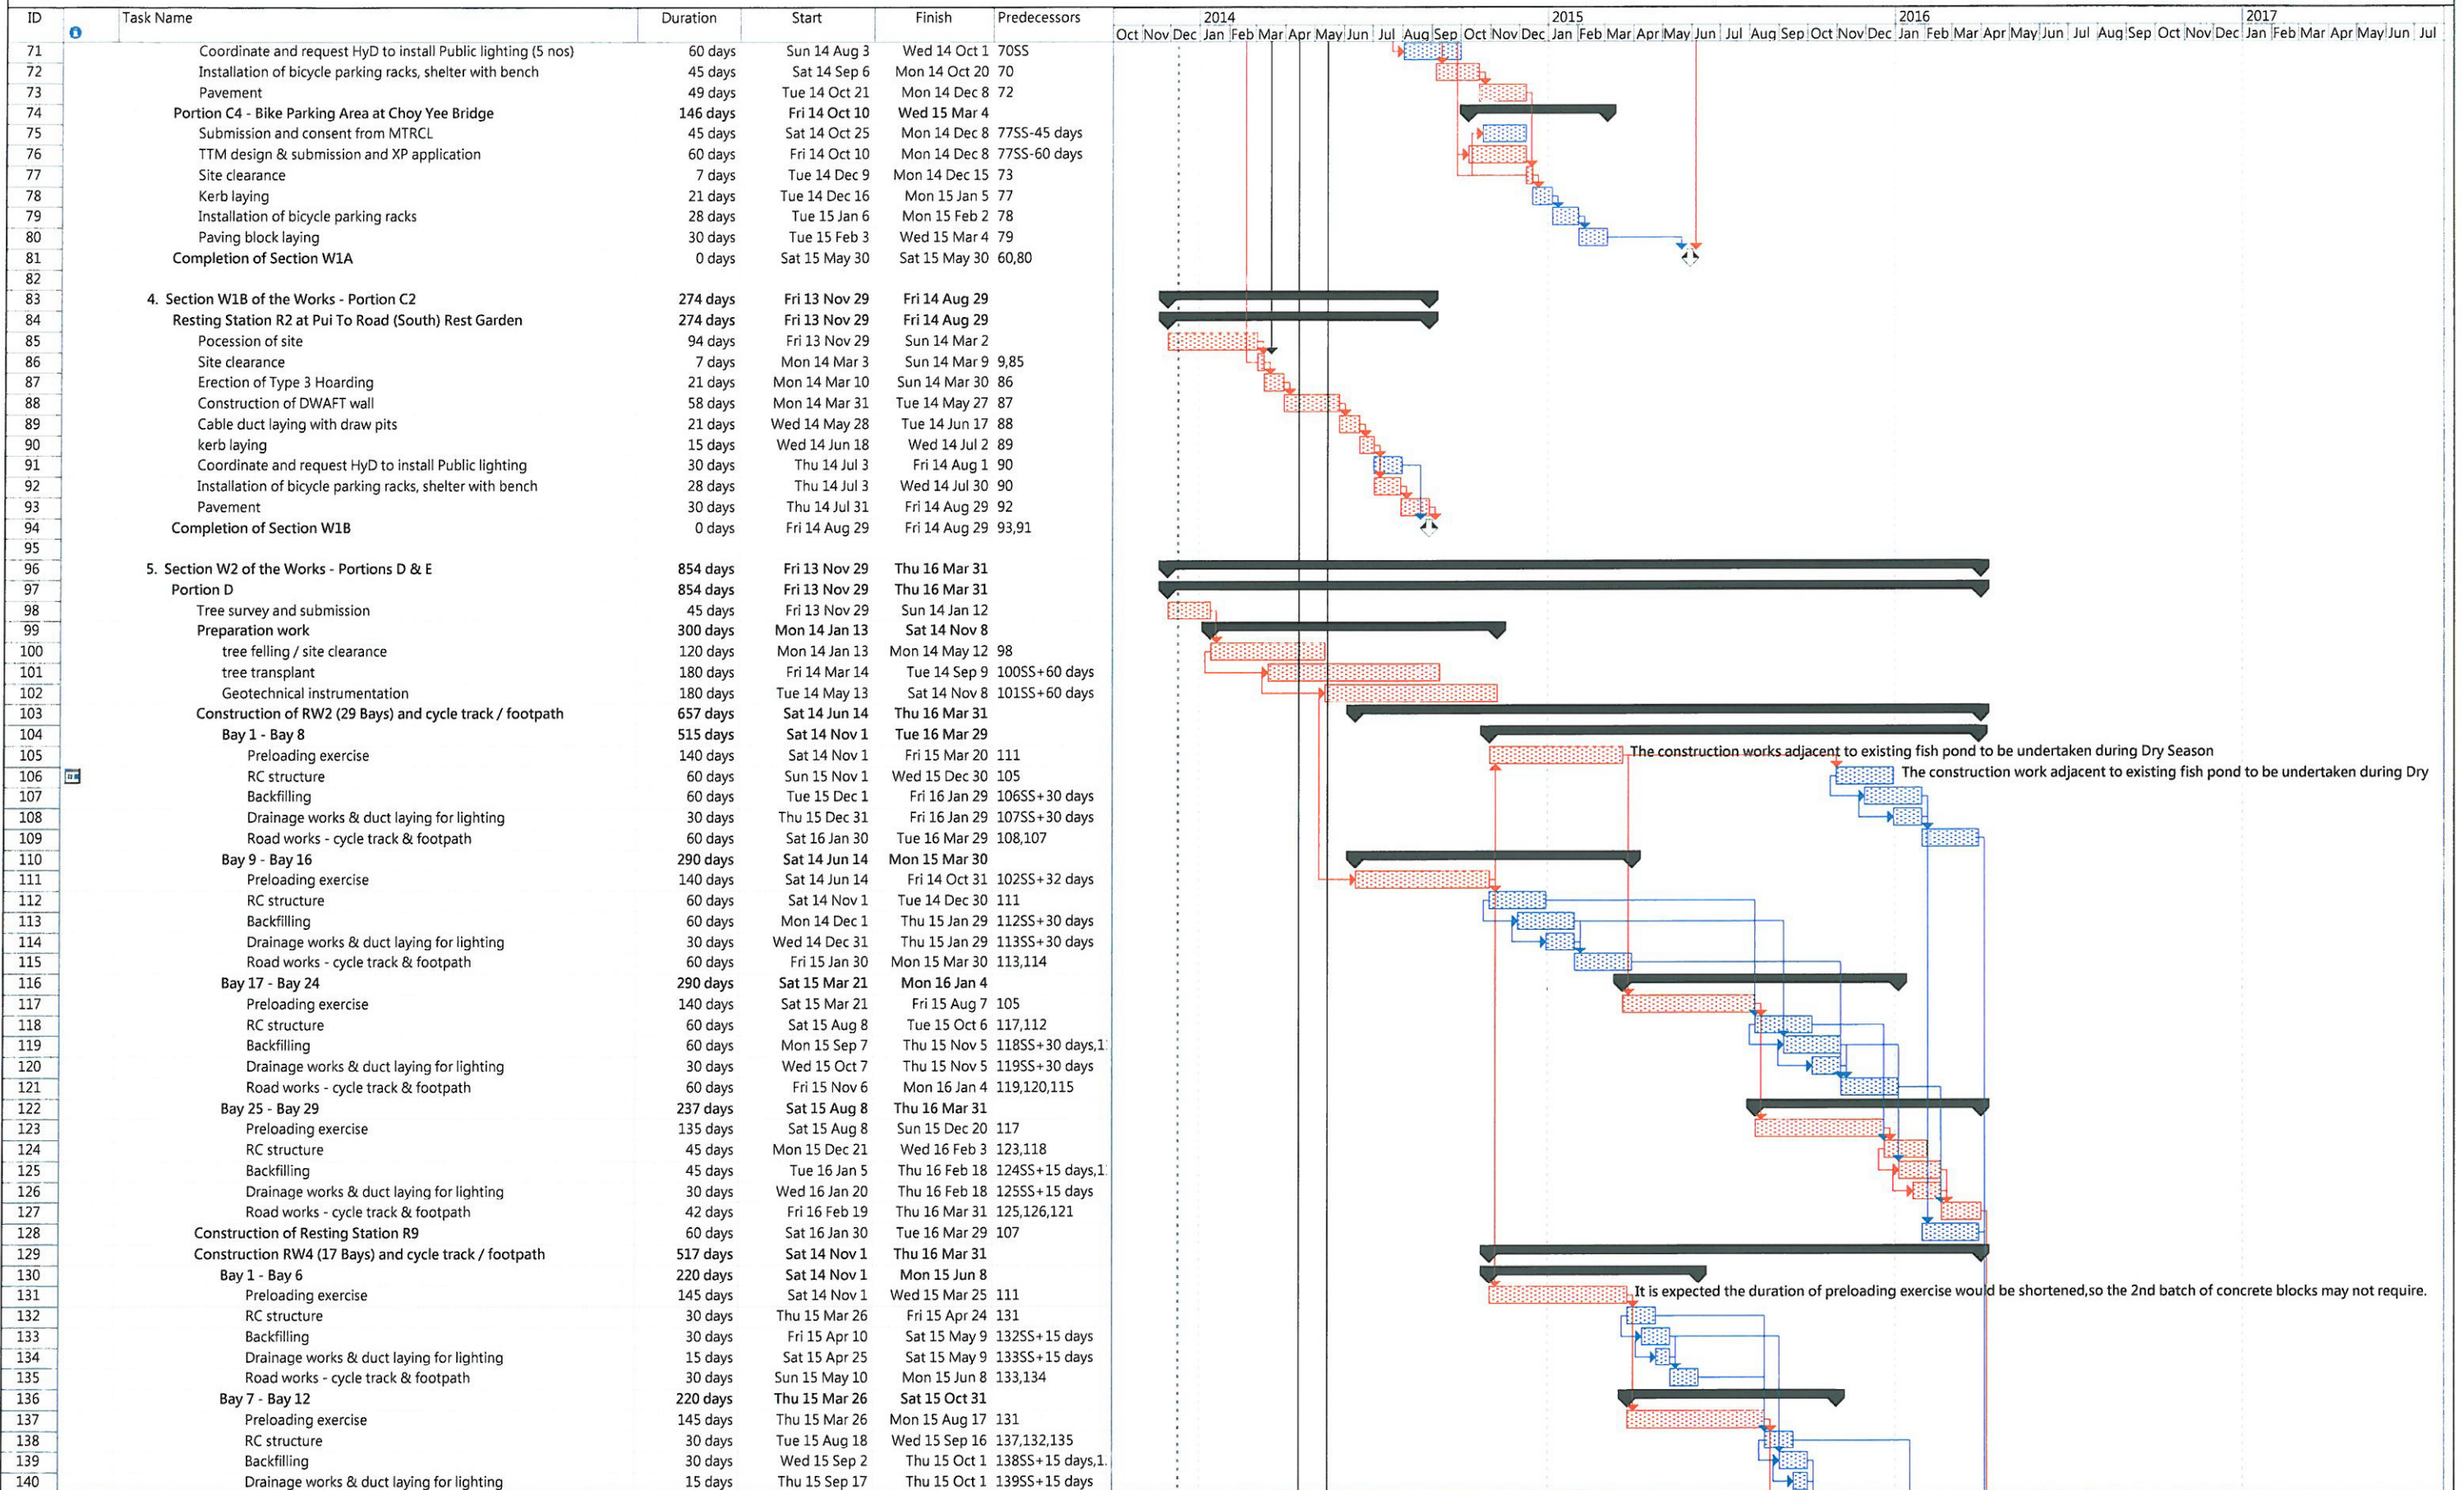

Project: YL/2013/01
Data Date: 29 Nov 2013
Submission: 09 Dec 2013


Task: Progress (blue dotted), Milestone (red dotted), Critical Task (black diamond), Summary (black bar), Rolled Up Task (black bar with arrow), Rolled Up Milestone (blue dotted bar with arrow), Split (white diamond), External Tasks (grey bar), Group By Summary (grey bar with arrow), Deadline (grey bar with arrow)

Cycle Tracks from Tuen Mun to Sheugn Shui - Stage 1
Project Programme of the Works

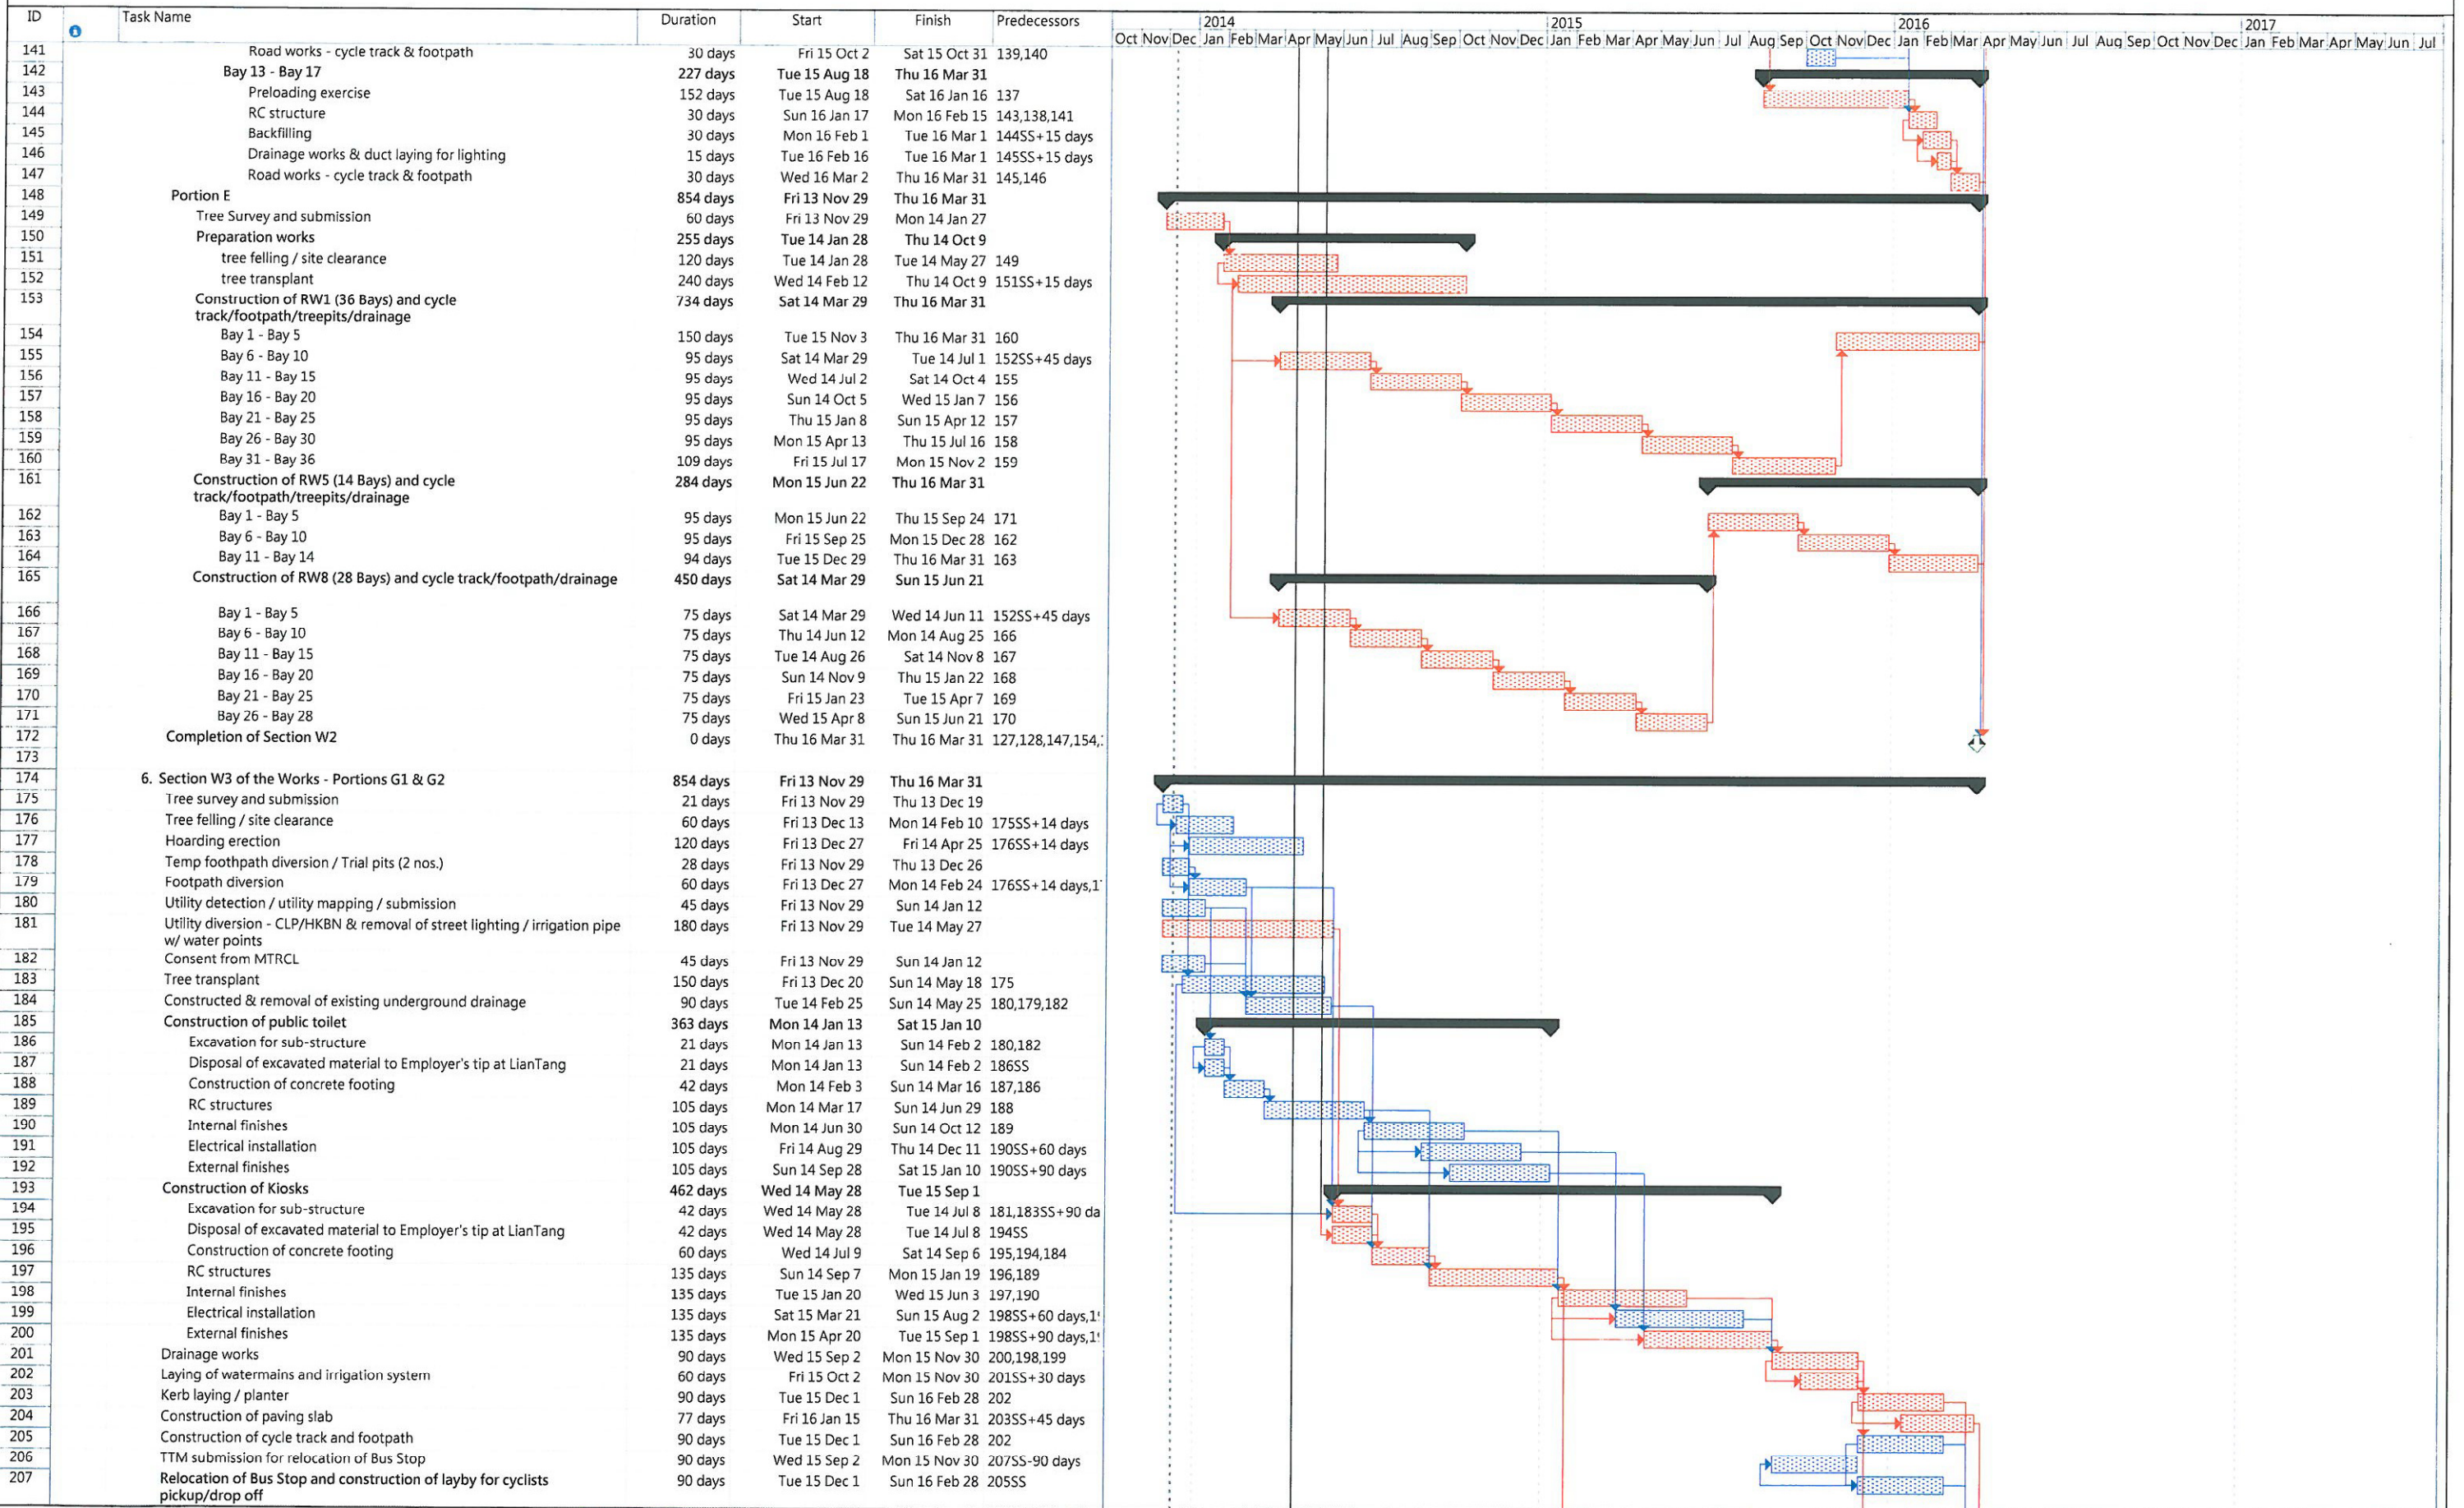

Cycle Tracks from Tuen Mun to Sheugn Shui - Stage 1

Project Programme of the Works

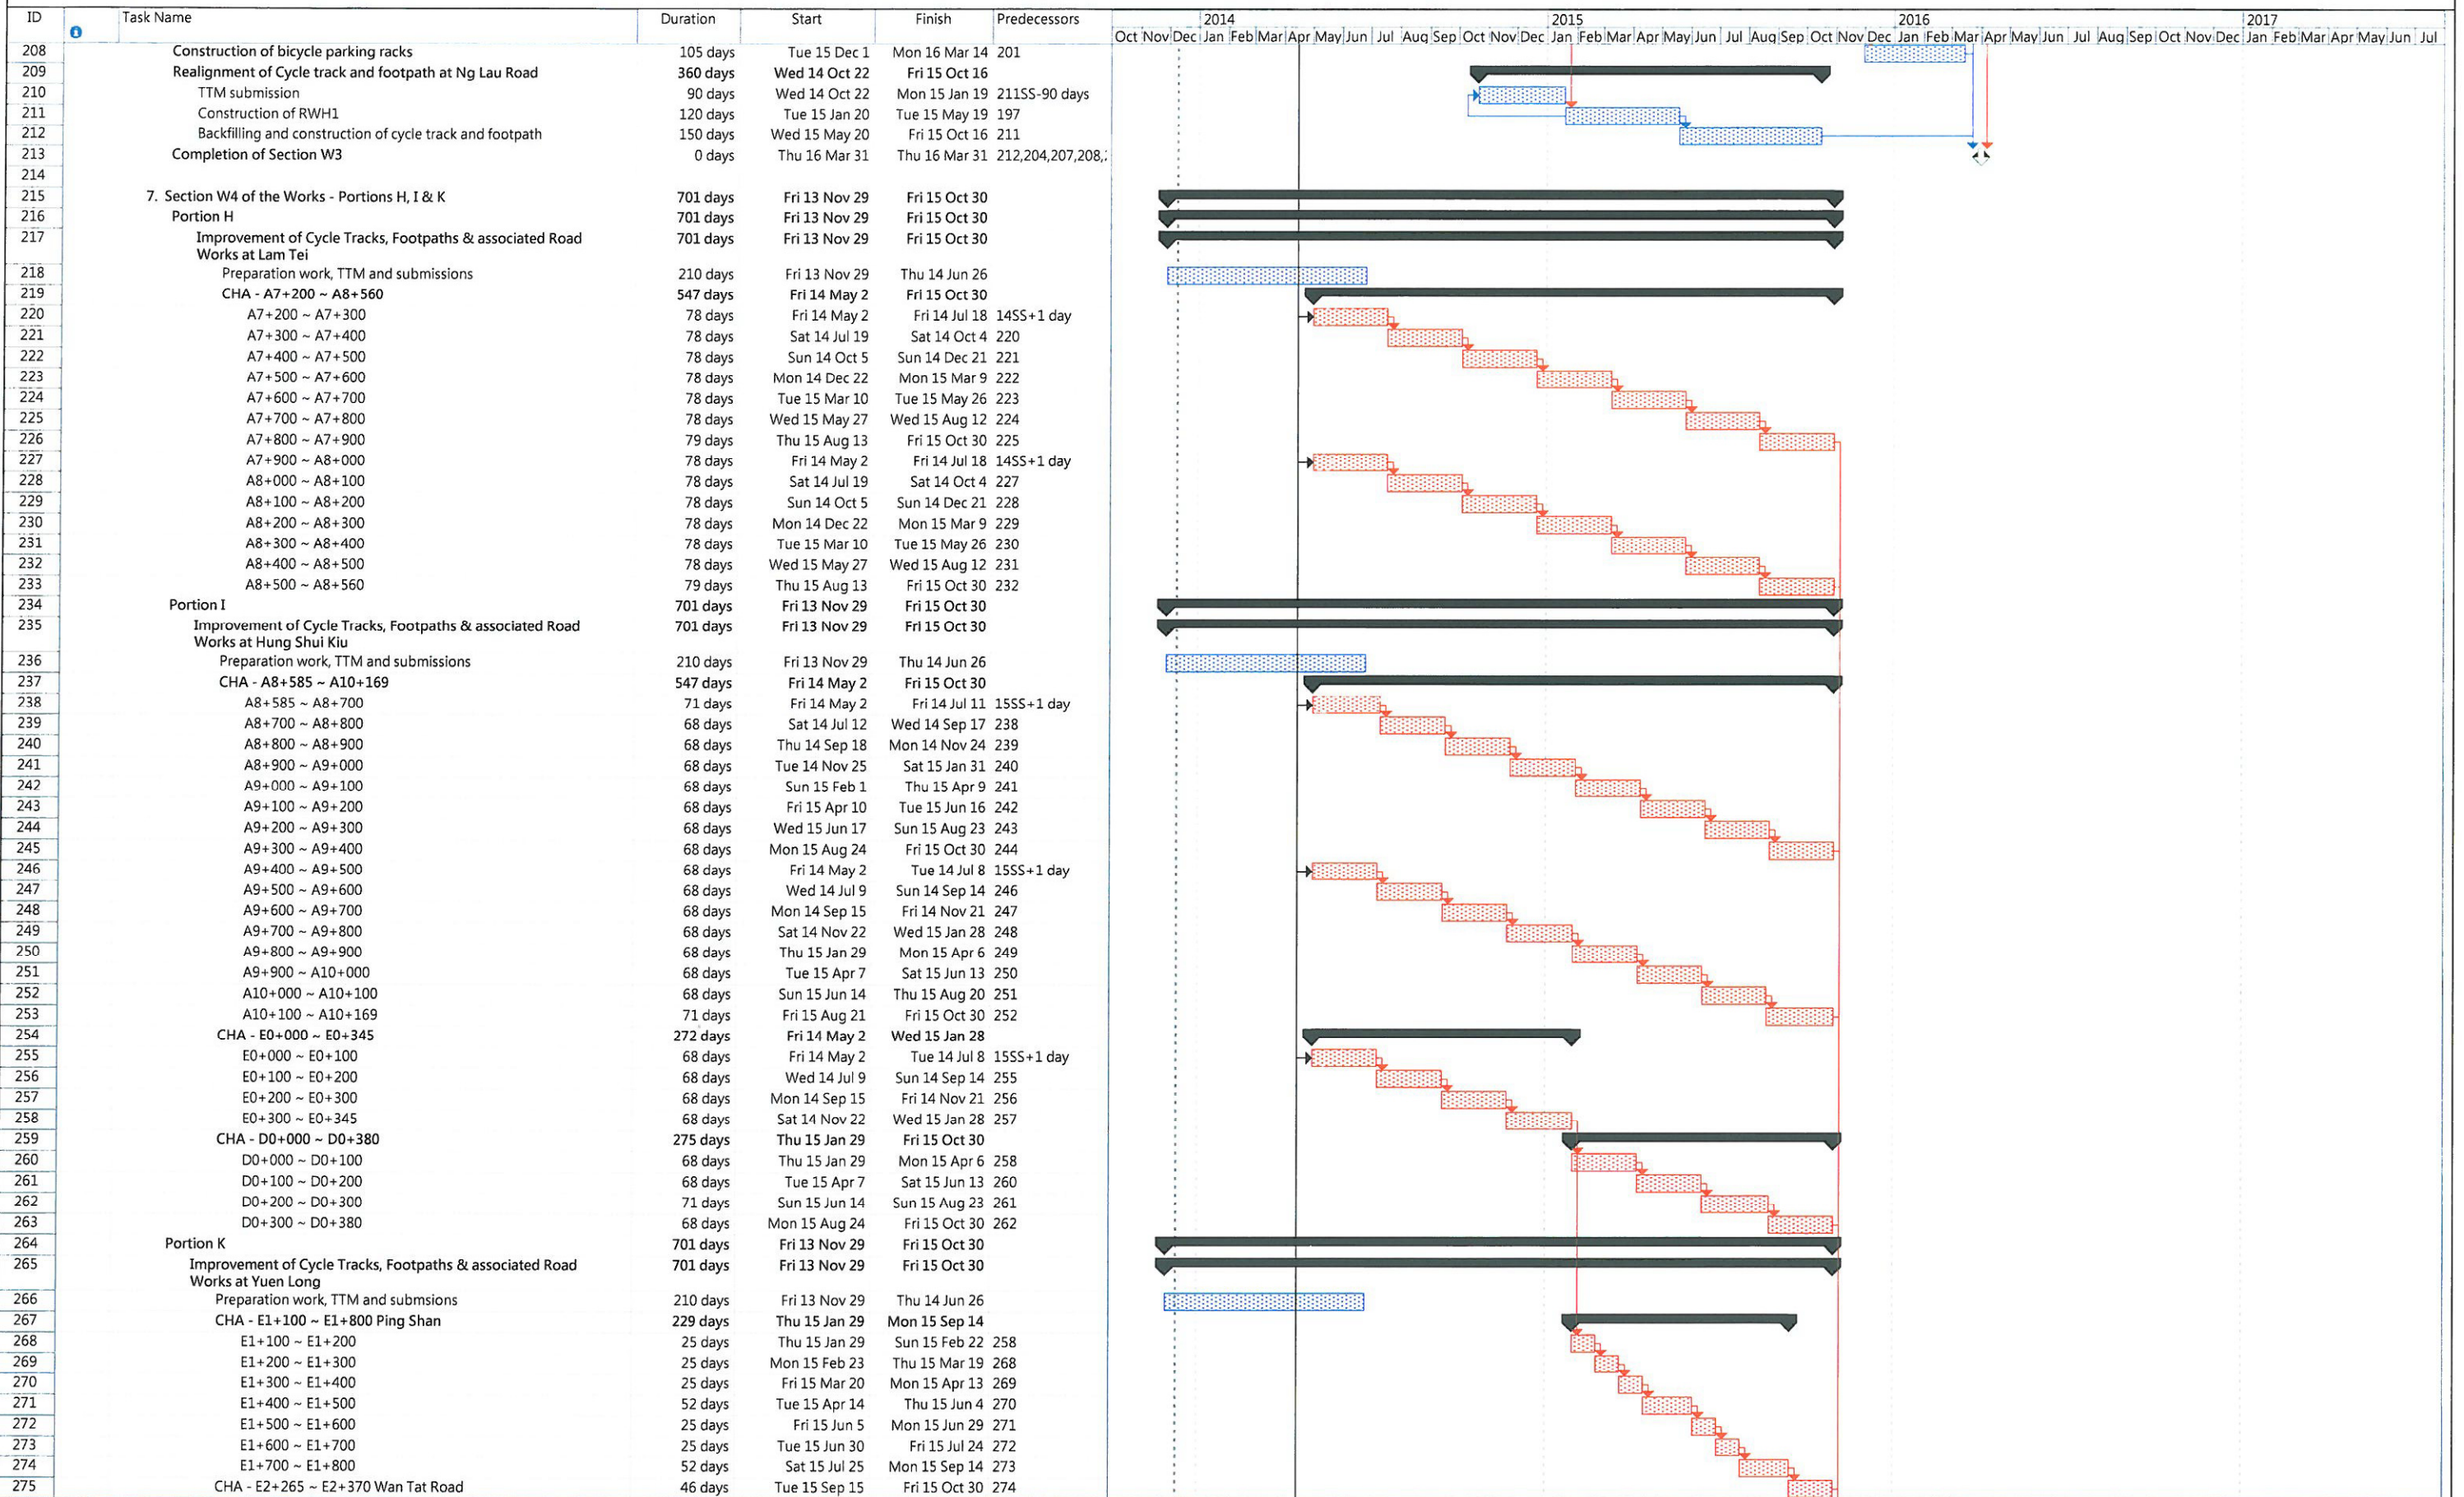

Cycle Tracks from Tuen Mun to Sheugn Shui - Stage 1
Project Programme of the Works


| ID | Task Name | Duration | Start | Finish | Predecessors | 2014 | 2015 | 2016 | 2017 |
|-----|---|----------|---------------|---------------|---------------------|---|------|------|------|
| | | | | | | Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul | | | |
| 276 | CHA - m0+00 ~ m0+200 YOHO Town Phase 3 Development | 125 days | Mon 14 Oct 13 | Sat 15 Feb 14 | 282 | | | | |
| 277 | CHA - E5+840 ~ E5+915 Pok Io | 50 days | Sun 15 Feb 15 | Sun 15 Apr 15 | 276 | | | | |
| 278 | Stream Decking STR1 | 240 days | Thu 14 May 1 | Fri 14 Dec 15 | | | | | |
| 279 | Submission and consent from MTRCL | 30 days | Thu 14 May 1 | Fri 14 May 30 | 175S | | | | |
| 280 | ELS / Excavation | 60 days | Sat 14 May 31 | Tue 14 Jul 29 | 279 | | | | |
| 281 | Base slab | 30 days | Wed 14 Jul 30 | Thu 14 Aug 28 | 280 | | | | |
| 282 | Wall and top Slab | 45 days | Fri 14 Aug 29 | Sun 14 Oct 12 | 281 | | | | |
| 283 | Railing | 45 days | Mon 14 Oct 13 | Wed 14 Nov 26 | 282 | | | | |
| 284 | Road works / Pavement | 30 days | Thu 14 Nov 27 | Fri 14 Dec 26 | 283 | | | | |
| 285 | Resting Station R4 | 208 days | Mon 15 Apr 6 | Fri 15 Oct 30 | | | | | |
| 286 | Tree survey and submission | 14 days | Mon 15 Apr 6 | Sun 15 Apr 19 | 277 | | | | |
| 287 | Site clearance | 7 days | Mon 15 Apr 20 | Sun 15 Apr 26 | 286 | | | | |
| 288 | Erection of temporary chain-link fence | 14 days | Mon 15 Apr 27 | Sun 15 May 10 | 287 | | | | |
| 289 | Tree felling | 7 days | Mon 15 May 11 | Sun 15 May 17 | 288 | | | | |
| 290 | Drainage works | 21 days | Mon 15 May 18 | Sun 15 Jun 7 | 289 | | | | |
| 291 | Cable duct laying with draw pits | 25 days | Mon 15 Jun 8 | Thu 15 Jul 2 | 290 | | | | |
| 292 | Installation of irrigation pipe and irrigation point (3 nos.) | 25 days | Mon 15 Jun 8 | Thu 15 Jul 2 | 290 | | | | |
| 293 | Kerb laying | 30 days | Fri 15 Jul 3 | Sat 15 Aug 1 | 291,292 | | | | |
| 294 | Coordinate and request HyD to install Public lighting (4 nos) | 60 days | Fri 15 Jul 3 | Mon 15 Aug 31 | 293SS | | | | |
| 295 | Installation of bicycle parking racks, shelter with bench | 45 days | Sun 15 Aug 2 | Tue 15 Sep 15 | 293 | | | | |
| 296 | Pavement | 45 days | Wed 15 Sep 16 | Fri 15 Oct 30 | 295 | | | | |
| 297 | Completion of Section W4 | 0 days | Fri 15 Oct 30 | Fri 15 Oct 30 | 226,233,245,253,296 | | | | |
| 298 | | | | | | | | | |
| 299 | 8. Section W5 of the Works - Portion J | 854 days | Fri 13 Nov 29 | Thu 16 Mar 31 | | | | | |
| 300 | Tree survey and submission | 14 days | Fri 13 Nov 29 | Thu 13 Dec 12 | | | | | |
| 301 | Tree felling / site clearance | 14 days | Fri 13 Dec 6 | Thu 13 Dec 19 | 300SS+7 days | | | | |
| 302 | Hoarding erection | 90 days | Fri 13 Dec 20 | Wed 14 Mar 19 | 301 | | | | |
| 303 | Trial pits (4 nos.) | 48 days | Fri 13 Nov 29 | Wed 14 Jan 15 | | | | | |
| 304 | Utility detection / detection of existing DN1000 rising main sewer / utility mapping / submission | 30 days | Fri 13 Nov 29 | Sat 13 Dec 28 | | | | | |
| 305 | Utility diversion - gas main & PCCW cable by others | 90 days | Sun 13 Dec 29 | Fri 14 Mar 28 | 304 | | | | |
| 306 | Tree transplant | 90 days | Fri 13 Dec 13 | Wed 14 Mar 12 | 300 | | | | |
| 307 | Construction of food kiosk and metter room | 426 days | Mon 14 Feb 3 | Sat 15 Apr 4 | | | | | |
| 308 | Excavation for sub-structure | 21 days | Mon 14 Feb 3 | Sun 14 Feb 23 | 302SS+45 days,31 | | | | |
| 309 | Disposal of excavated material to Employer's tip at LianTang and DSD Contract DC/2010/02 | 21 days | Mon 14 Feb 3 | Sun 14 Feb 23 | 308SS | | | | |
| 310 | Construction of concrete footing | 45 days | Mon 14 Feb 24 | Wed 14 Apr 9 | 309,308 | | | | |
| 311 | RC structures | 150 days | Thu 14 Apr 10 | Sat 14 Sep 6 | 310 | | | | |
| 312 | Internal finishes | 120 days | Sun 14 Sep 7 | Sun 15 Jan 4 | 311 | | | | |
| 313 | Electrical installation | 120 days | Thu 14 Nov 6 | Thu 15 Mar 5 | 312SS+60 days | | | | |
| 314 | External finishes | 120 days | Sat 14 Dec 6 | Sat 15 Apr 4 | 312SS+90 days | | | | |
| 315 | Construction of first aid and cycle rental kiosks | 426 days | Sat 14 Mar 29 | Thu 15 May 28 | | | | | |
| 316 | Excavation for sub-structure | 21 days | Sat 14 Mar 29 | Fri 14 Apr 18 | 302SS+60 days,31 | | | | |
| 317 | Disposal of excavated material to Employer's tip at LianTang and DSD Contract DC/2010/02 | 21 days | Sat 14 Mar 29 | Fri 14 Apr 18 | 316SS | | | | |
| 318 | Construction of concrete footing | 45 days | Sat 14 Apr 19 | Mon 14 Jun 2 | 317,316,310 | | | | |
| 319 | RC structures | 150 days | Tue 14 Jun 3 | Thu 14 Oct 30 | 318 | | | | |
| 320 | Internal finishes | 120 days | Fri 14 Oct 31 | Fri 15 Feb 27 | 319 | | | | |
| 321 | Electrical installation | 120 days | Tue 14 Dec 30 | Tue 15 Apr 28 | 320SS+60 days | | | | |
| 322 | External finishes | 120 days | Thu 15 Jan 29 | Thu 15 May 28 | 320SS+90 days | | | | |
| 323 | Construction of public toilet | 426 days | Mon 14 Apr 28 | Sat 15 Jun 27 | | | | | |
| 324 | Excavation for sub-structure | 21 days | Mon 14 Apr 28 | Sun 14 May 18 | 316SS+30 days | | | | |
| 325 | Disposal of excavated material to Employer's tip at LianTang and DSD Contract DC/2010/02 | 21 days | Mon 14 Apr 28 | Sun 14 May 18 | 324SS | | | | |
| 326 | Construction of concrete footing | 45 days | Mon 14 May 19 | Wed 14 Jul 2 | 325,324,310 | | | | |
| 327 | RC structures | 150 days | Thu 14 Jul 3 | Sat 14 Nov 29 | 326 | | | | |
| 328 | Internal finishes | 120 days | Sun 14 Nov 30 | Sun 15 Mar 29 | 327 | | | | |
| 329 | Electrical installation | 120 days | Thu 15 Jan 29 | Thu 15 May 28 | 328SS+60 days | | | | |
| 330 | External finishes | 120 days | Sat 15 Feb 28 | Sat 15 Jun 27 | 328SS+90 days | | | | |
| 331 | Drainage works | 90 days | Sun 15 Jun 28 | Fri 15 Sep 25 | 314,322,330,312,331 | | | | |
| 332 | Laying of watermain and irrigation system | 60 days | Tue 15 Jul 28 | Fri 15 Sep 25 | 331SS+30 days | | | | |
| 333 | Kerb laying / planter | 120 days | Sat 15 Sep 26 | Sat 16 Jan 23 | 332,331 | | | | |
| 334 | Construction of paving slab | 128 days | Wed 15 Nov 25 | Thu 16 Mar 31 | 333SS+60 days | | | | |
| 335 | Completion of Section W5 | 0 days | Thu 16 Mar 31 | Thu 16 Mar 31 | 334 | | | | |
| 336 | | | | | | | | | |
| 337 | 9. Section W7 of the Works - Portion M | 639 days | Fri 13 Nov 29 | Sat 15 Aug 29 | | | | | |
| 338 | Cycle Tracks, Footpaths & associated Road Works at Kam Tin River | 639 days | Fri 13 Nov 29 | Sat 15 Aug 29 | | | | | |
| 339 | CH - MP0+000 ~ MP1+100 | 639 days | Fri 13 Nov 29 | Sat 15 Aug 29 | | | | | |
| 340 | Tree survey and submission | 45 days | Fri 13 Nov 29 | Sun 14 Jan 12 | | | | | |
| 341 | Tree Transplant | 150 days | Mon 14 Jan 13 | Wed 14 Jun 11 | 340 | | | | |
| 342 | Construction of cycle track / footpath | 504 days | Sun 14 Apr 13 | Sat 15 Aug 29 | | | | | |

Project: YL/2013/01
Data Date: 29 Nov 2013
Submission: 09 Dec 2013

Task: Progress Summary Rolled Up Critical Task Rolled Up Progress External Tasks Group By Summary Deadline

Critical Task: Milestone Rolled Up Task Rolled Up Milestone Split Project Summary Deadline

Cycle Tracks from Tuen Mun to Sheugn Shui - Stage 1
Project Programme of the Works

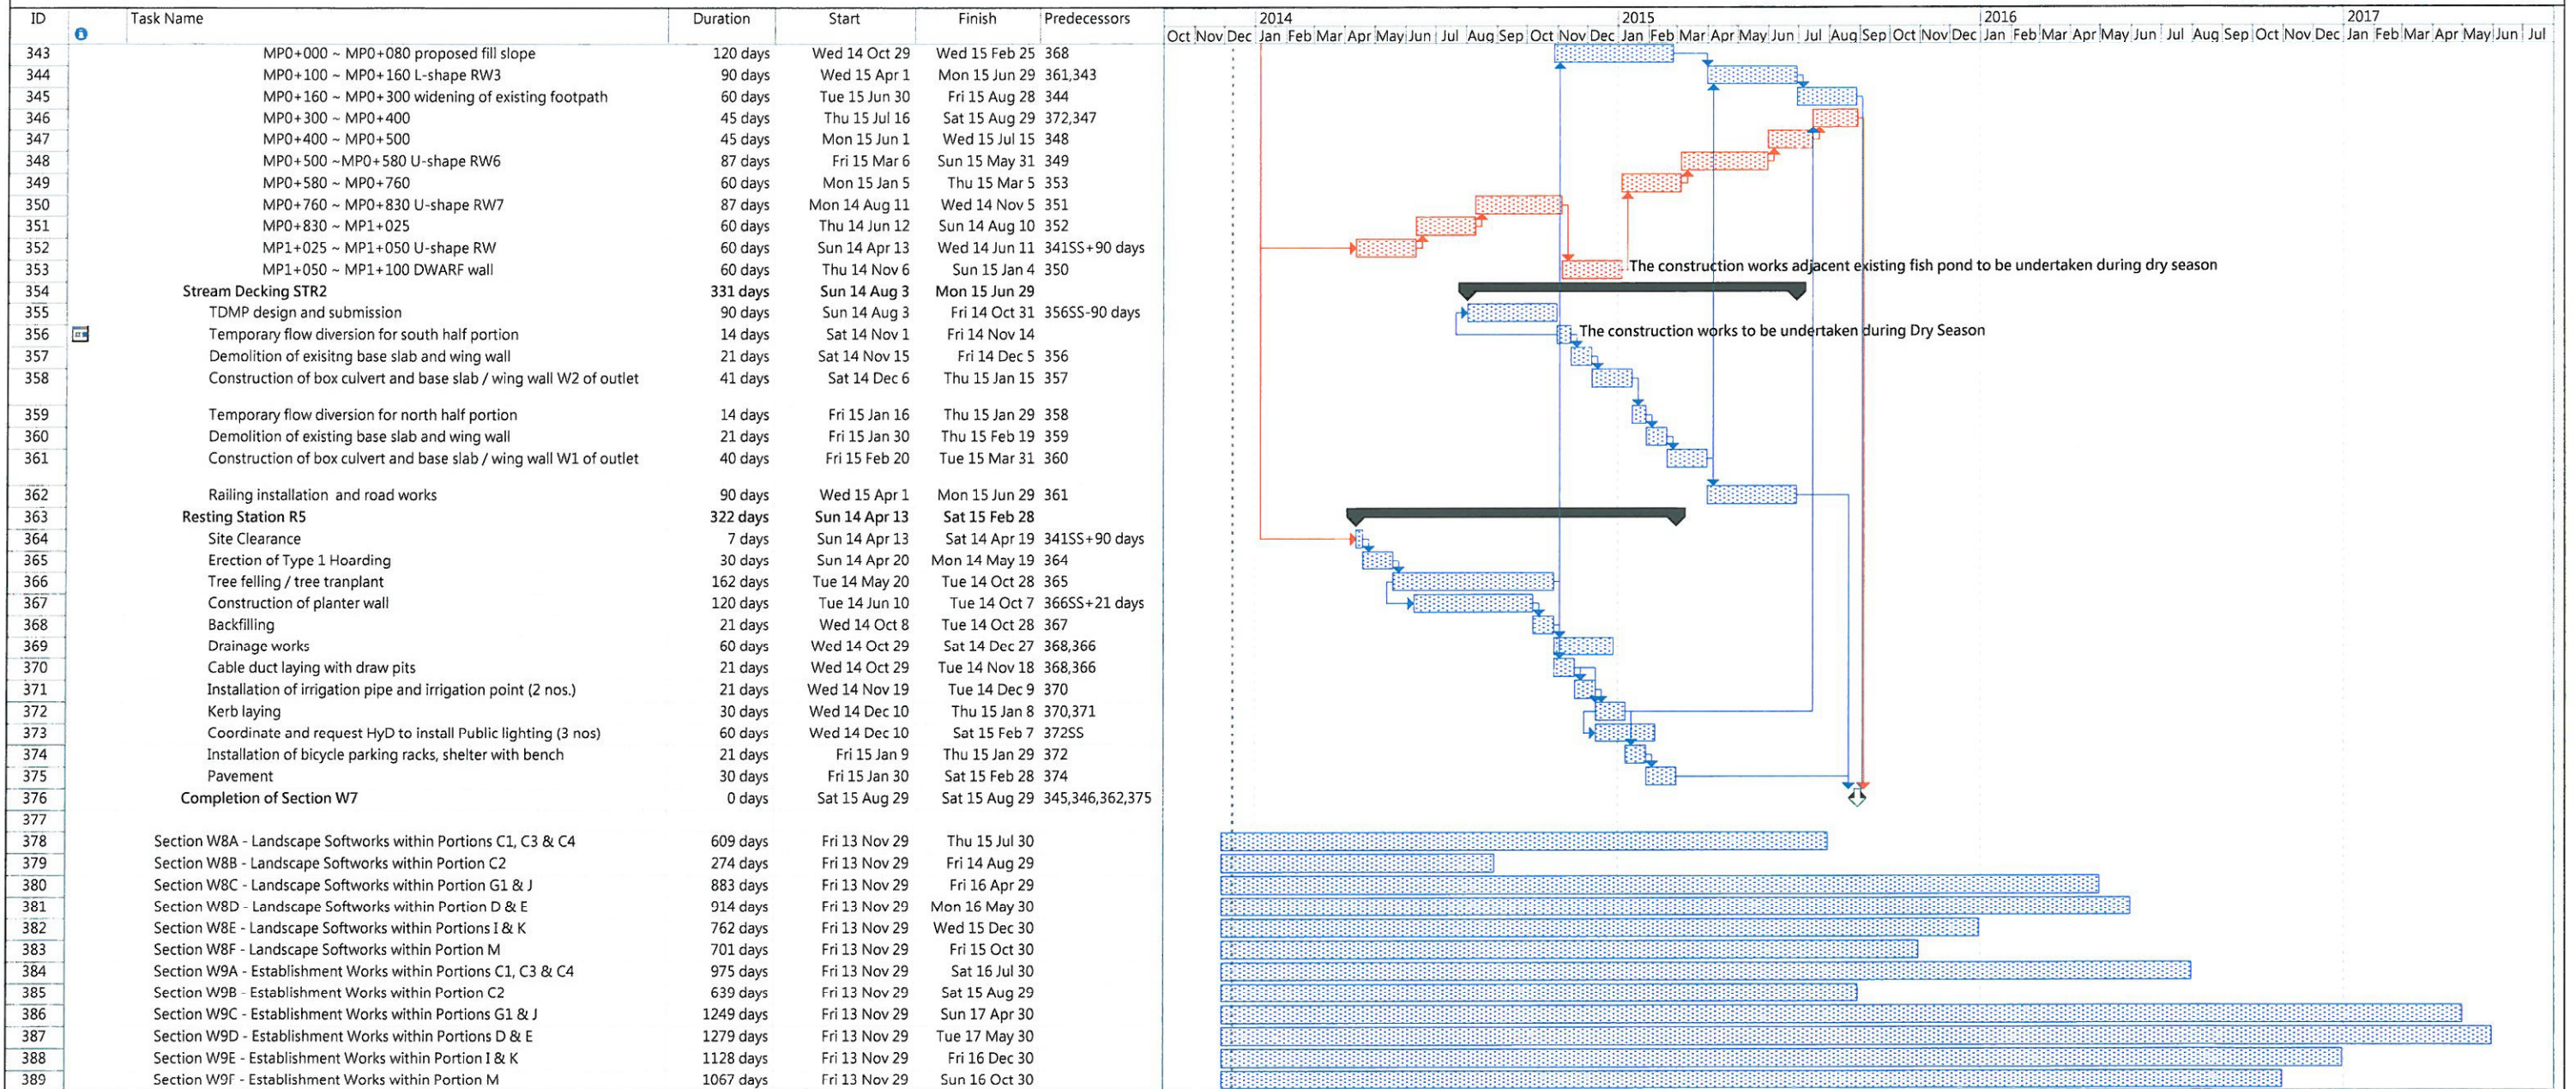

APPENDIX 3

THE CONTACT DETAILS OF KEY PERSONNEL OF THE PROJECT

Contact Details of Key Personnel for the Project

| Company / Department | Name | Position | Telephone |
|---|------------------|-----------------------------------|---------------------------------------|
| AECOM Consulting Services Limited (former URS Hong Kong Ltd.) | Mr. Rodney Ip | Environmental Team Leader | 2410 3750 |
| AECOM Consulting Services Limited (former URS Hong Kong Ltd.) | Mr. Vincent Kwan | Resident Engineer | 2672 7938 |
| Sang Hing – Kuly Joint Venture | Mr. Jeff Chan | Project Manager | 9606 2398 |
| Sang Hing – Kuly Joint Venture | Mr. W.K. Tang | Site Agent | 9300 7037 / 5638 3186 (Hotline) |
| Sang Hing – Kuly Joint Venture | Mr. Michael Wan | Site Environmental Officer | 9222 3089 |
| Fugro Hong Kong Ltd. | Mr. Colin Yung | Independent Environmental Checker | 3565 4114 |

APPENDIX 4

IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES

Table A1-1 Air Quality Impact – Implementation Schedule of Recommended Mitigation Measures

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location / Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|---------------------------|-----------|---|---|--------------------------------|---|--|
| Construction Phase | | | | | | |
| S.3.6.2 | S.3.2.3 | All the dust control measures as recommended in the Air Pollution Control (Construction Dust) Regulation, where applicable, should be implemented. Typical dust control measures include: | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |
| S.3.6.2 | S.3.2.3 | <ul style="list-style-type: none"> The works area for site clearance shall be sprayed with water before, during and after the operation so as to maintain the entire surface wet | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |
| S.3.6.2 | S.3.2.3 | <ul style="list-style-type: none"> Restricting heights from which materials are to be dropped, as far as practicable to minimize the fugitive dust arising from unloading/ loading | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |
| S.3.6.2 | S.3.2.3 | <ul style="list-style-type: none"> Immediately before leaving a construction site, all vehicles shall be washed to remove any dusty materials from the bodies and wheels. However, all spraying of materials and surfaces should avoid excessive water usage | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |
| S.3.6.2 | S.3.2.3 | <ul style="list-style-type: none"> Where a vehicle leaving a construction site is carrying a load of dusty materials, the load shall be covered entirely by clean impervious sheeting to ensure that the dusty materials will not leak from the vehicle | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |
| S.3.6.2 | S.3.2.3 | <ul style="list-style-type: none"> Travelling speeds should be controlled to reduce traffic induced dust dispersion and re-suspension within the site from the operating haul trucks | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |
| S.3.6.2 | S.3.2.3 | <ul style="list-style-type: none"> Erection of hoarding of not less than 2.4 m high from ground level along the site boundary, where appropriate | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |
| S.3.6.2 | S.3.2.3 | <ul style="list-style-type: none"> Any stockpile of dusty materials shall be covered entirely by impervious sheeting; and/or placed in an area sheltered on the top and 4 sides | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location / Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|-------------------|-----------|--|---|--------------------------------|---|--|
| S.3.6.2 | S.3.2.3 | <ul style="list-style-type: none"> All dusty materials shall be sprayed with water or a dust suppression chemical immediately prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet | Air Quality (fugitive dust) Control during Construction Phase | Contractors | At all construction areas of the site during the entire construction period | Annex 4 and Annex 12 of EIAO -TM, Air Pollution Control (Construction Dust) Regulation |
| Operational Phase | | | | | | |
| N/A | N/A | None specific | N/A | N/A | N/A | N/A |

Table A1-2 Noise Impact – Implementation Schedule of Recommended Mitigation Measures

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location / Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|--------------------|-----------|--|---|--------------------------------|--|---|
| Construction Phase | | | | | | |
| S.5.5.11 | S.4.2.17 | In order to prevent potential cumulative construction noise impacts to NSRs at Mai Po San Tsuen and Palm Springs, the works at the cycle track section (near CH-MP5+100m) are recommended to be scheduled to avoid works at the areas near Castle Peak Road of the Proposed Comprehensive Development at Wo Shang Wai (CDWSW) project if the works site of the CDWSW project is less than 300 m away from Castle Peak Road. | Noise control during construction | Contractors, ER | Construction areas near the specified locations during the construction period | EIA, Contractual requirements |
| S.5.5.14 | S.4.2.17 | The contractor shall liaise with the Yuen Long and Kam Tin Sewerage and Sewage Disposal Stage 2 (YLKTSSD2) and North West New Territories Salt Water Supply (NWNTSWS) works contractors so as to avoid undertaking works concurrently with the works when they are in the close proximity as far as practicable. As a conservative approach, works for the cycle track shall be carried out when the works from the other projects are over 300 m away. The requirements shall be included in the works contracts. | Noise control during construction | Contractors, ER | Construction areas near the specified locations during the construction period | EIA, Contractual requirements |
| Table 5-7 | S.4.2.19 | Use of quiet plant (PME): <ul style="list-style-type: none"> - mini excavator - mobile crane - dump truck - hand-held electric circular saw - concrete lorry mixer - lorry - vibratory poker - asphalt paver - crane mounted auger - road roller - road ripper, excavator mounted | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | EIA, Contractual requirements |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location / Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|----------------------|-----------|---|---|--------------------------------|--|---|
| S.5.6.2 Table 5-8 | S.4.2.19 | Noise barrier in the form of site hoarding shall be used for the following PMEs where practicable: <ul style="list-style-type: none"> - mini excavator - mobile crane - dump truck - hand-held electric circular saw - bar bender - vibrating hammer - generator - concrete lorry mixer - lorry - vibratory poker - asphalt paver - compactor - road roller - crane mounted auger - grout mixer - grout pump - drill - road ripper, excavator mounted | Noise control during construction | Contractors | At all construction areas of the site close to identified NSRs during the entire construction period | EIA, Contractual requirements |
| S.5.6.2 | S.4.2.19 | Noise enclosure shall be used for the following PMEs where practicable: <ul style="list-style-type: none"> - air compressor - hand-held breaker | Noise control during construction | Contractors | At all construction areas of the site close to identified NSRs during the entire construction period | EIA, Contractual requirements |
| S.5.6.2 | S.4.2.19 | The barrier / enclosure material's surface mass shall be in excess of 7 kg/m ² . | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | EIA, Contractual requirements |
| S.5.6.6 | S.4.2.19 | Use of alternative quieter plant such as road ripper, excavator mounted instead of handheld breaker during levelling/excavation works. | Noise control during construction | Contractors | At construction areas of the site close to NSR12 and NSR20 during the entire construction period | EIA, Contractual requirements |
| S.5.6.8 | S.4.2.19 | The Contractor shall adopt the Code of Practice on Good Management Practice to Prevent Violation of the Noise Control Ordinance (Chapter 400) (for Construction Industry) published by EPD | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |
| S.5.6.8 | S.4.2.19 | The Contractor shall observe and comply with the statutory and non-statutory requirements and guidelines | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location / Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|-------------------|-----------|---|---|--------------------------------|---|---|
| S.5.6.8 | S.4.2.19 | Before commencing any work, the Contractor shall submit to the project Engineer for approval the method of working, equipment and noise mitigation measures intended to be used at the site | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |
| S.5.6.8 | S.4.2.19 | The Contractor shall devise and execute working methods to minimize the noise impact on the surrounding sensitive uses, and provide experienced personnel with suitable training to ensure that those methods are implemented | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |
| S.5.6.8 | S.4.2.19 | Noisy equipment and noisy activities should be located as far away from the NSRs as is practical | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |
| S.5.6.8 | S.4.2.19 | Unused equipment should be turned off. PME should be kept to a minimum and the parallel use of noisy equipment / machinery should be avoided | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |
| S.5.6.8 | S.4.2.19 | Regular maintenance of all plant and equipment | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |
| S.5.6.8 | S.4.2.19 | Material stockpiles and other structures should be effectively utilised as noise barriers, where practicable | Noise control during construction | Contractors | At all construction areas of the site during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |
| S.5.6.8 | S.4.2.19 | The Contractor shall liaise with the schools that are located near the works sites regarding their examination period and schedule the noisy works to avoid the examination period as far as possible | Noise control during construction | Contractors | At construction areas near schools during the entire construction period | Annex 5 and Annex 13 of EIAO-TM |
| Operational Phase | | | | | | |
| N/A | N/A | None specific | N/A | N/A | N/A | N/A |

Table A1-3 Water Quality Impact – Implementation Schedule of Recommended Mitigation Measures

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location / Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|--------------------|-----------|---|---|--------------------------------|---|---|
| Construction Phase | | | | | | |
| S. 6.6.1 | S.5.2.4 | Mitigation measures should be implemented to prevent the uncontrolled discharge of wastewater from the construction site in accordance with Practice Note for Professional Persons ProPECC PN1/94 - Construction Site Drainage | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | ProPECC PN1/94, Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Surface run-off from the construction sites will be directed into storm drains via adequately designed wastewater treatment facilities such as sand traps, silt traps and sediment settling basins. This is important for works immediately along the Kam Tin River, Ngau Tam Mei Main Drainage Channel, River Beas and Shek Sheung River | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Channels, earth bunds or sand bag barriers will be provided on-site to properly direct stormwater to the above-mentioned facilities | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Existing silt removal facilities, channels and manholes along roads and pedestrian walkways will be maintained and the deposited silt and grit will be removed regularly, at the onset of and after each rainstorm to ensure that these facilities are functioning properly at all times | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Other manholes (including any newly constructed ones) will be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Open stockpiles of materials on site will be avoided or where unavoidable covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Where possible, works entailing soil excavation will be minimized during the rainy season (i.e. April to September); | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Where applicable, final earthworks surfaces/ slopes will be well compacted and hydro-seeded following completion to prevent | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire | Water Pollution Control Ordinance |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location / Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|----------|-----------|--|---|--------------------------------|---|---|
| | | erosion | | | construction period | |
| S. 6.6.1 | S.5.2.4 | During construction works, chemical toilets will be provided for the use of site staff. These will be provided by a licensed contractor, who will be responsible for appropriate disposal and maintenance of the effluent | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Works adjacent to the fishponds near Kam Tin River inside the conservation area (CA) and Mai Po San Tsuen should be avoided as far as possible during the wet season to avoid runoff into the fishponds | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Wastewater from site facilities (such as toilets) should be discharged to foul sewer, where available. Chemical toilets will be considered where there is no foul sewer connection. There is not expected to be a temporary canteen. | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | All site discharges within Water Control Zones must comply with the terms and conditions of a valid discharge licence issued by EPD | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Vehicle wheel washing facilities should be provided, where applicable, at the site exit such that mud, debris, etc. deposited onto the vehicle wheels or body can be washed off before the vehicles are leaving the site area | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Section of the road between the wheel washing bay and the public road should be paved with backfill to reduce vehicle tracking of soil and to prevent site run-off from entering public road drains | Stormwater and Non-point Source Pollution Control | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | The project may occasionally involve the handling of fuel and generates chemical wastes. It must be ensured that all fuel tanks and chemical storage are sited on sealed areas and provided with locks | Protection Against Accidental Spillage | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent accidentally spilled oil, fuel or chemicals from reaching the receiving waters | Protection Against Accidental Spillage | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |
| S. 6.6.1 | S.5.2.4 | Oil and grease removal facilities will be provided where appropriate, for example, in area near plant workshop/ maintenance areas | Protection Against Accidental Spillage | Contractors | At all construction areas of the site during the entire construction period | Water Pollution Control Ordinance |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location / Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|-------------------|-----------|--|---|--------------------------------|---|---|
| S. 6.6.1 | S.5.2.4 | Chemical waste arising from the site should be properly stored, handled, treated and disposed of in compliance with the requirements stipulated under the Waste Disposal (Chemical Waste) (General) Regulation | Protection Against Accidental Spillage | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal (Chemical Waste) (General) Regulation |
| Operational Phase | | | | | | |
| N/A | N/A | None specific | N/A | N/A | N/A | N/A |

Table A1-4 Waste Management Implication – Implementation Schedule of Recommended Mitigation Measures

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|--------------------|--------------------|--|---|--------------------------------|---|--|
| Construction Phase | | | | | | |
| S.7.4.1 | S. 6.2.1 – S.6.2.4 | An on-site environmental co-ordinator employed by the Contractor should be identified at the outset of the works. Prior to commencement of Project works, the co-ordinator shall prepare a WMP in accordance with the requirements set out in the ETWB TCW No. 19/2005, Waste Management on Construction Sites, for the ER's approval. The WMP shall include monthly and yearly Waste Flow Tables ("WFT") that indicate the amounts of waste generated, recycled and disposed of (including final disposal site), and which should be regularly updated; | Waste management during construction | Contractors | Prior to commencement of Project works, and implemented throughout the entire construction period | ETWB TCW No. 19/2005, Waste Management on Construction Sites |
| S.7.4.1 | S. 6.2.6 | Given the potential for secondary environmental impacts (dust, noise, water quality and visual impacts), mitigation measures are required to ensure proper handling, storage, transportation and disposal of materials at the outset and throughout the construction phase of the project | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> The reuse/ recycling of all materials on site shall be investigated and exhausted prior to treatment/ disposal off-site | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> Good site practices shall be adopted from the commencement of works to avoid the generation of waste, reduce cross contamination of waste and to promote waste minimisation | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> All waste materials shall be sorted on-site into inert and non-inert C&D materials, and where the materials can be recycled or reused, they shall be further segregated. Inert material, or public fill will comprise stone, rock, masonry, brick, concrete and soil which is suitable for land reclamation and site formation whilst non-inert materials include all other wastes generated from the construction process such as plastic packaging and vegetation (from site clearance). | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|----------|-----------|---|---|--------------------------------|---|--|
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> The Contractor shall be responsible for identifying what materials can be recycled/ reused, whether on-site or off-site. In the event of the latter, the Contractor shall make arrangements for the collection of the recyclable materials. Any remaining non-inert waste shall be collected and disposed of to the Public Filling Areas whilst any inert C&D materials shall be re-used on site as far as possible. Alternatively, if no use of the inert material can be found on-site, the materials can be delivered to a Public Fill Area or Public Fill Bank after obtaining the appropriate licence; | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> In order to monitor the disposal of C&D material and solid wastes at public filling facilities and landfills, and control fly-tipping, a trip-ticket system shall be implemented by the Contractor, in accordance with the contract and the requirements of WBTC 31/2004 "Trip Ticket System for Disposal of Construction and Demolition Material". | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | WBTC 31/2004 "Trip Ticket System for Disposal of Construction and Demolition Material" |
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> Under the Waste Disposal (Chemical Waste) (General) Regulation, the Contractor shall register as a Chemical Waste Producer if chemical wastes such as spent lubricants and paints are generated on site. Only licensed chemical waste collectors shall be employed to collect any chemical waste generated at site. The handling, storage, transportation and disposal of chemical wastes shall be conducted in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes and A Guide to the Chemical Waste Control Scheme both published by EPD; | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal (Chemical Waste) (General) Regulation |
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> A sufficient number of covered bins shall be provided on site for the containment of general refuse to prevent visual impacts and nuisance to the sensitive surroundings. These bins shall be cleared daily and the collected waste disposed of to the refuse transfer station. Further to the issue of ETWB TCW No. 6/2002A, Enhanced Specification for Site Cleanliness and Tidiness, the Contractor is required to maintain a clean and hygienic site throughout the project works; | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|--------------------------|-----------|--|---|--|---|---|
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> All chemical toilets, if any, shall be regularly cleaned and the night-soil collected and transported by a licensed contractor to a Government Sewage Treatment Works facility for disposal; and | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> Toolbox talks should be provided to workers about the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling. | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |
| S.7.4.1 | S. 6.2.6 | <ul style="list-style-type: none"> The Contractor shall comply with all relevant statutory requirements and guidelines and their updated versions that may be issued during the course of project construction. | Waste management during construction | Contractors | At all construction areas of the site during the entire construction period | Waste Disposal Ordinance |
| Operational Phase | | | | | | |
| S. 7.4.2 | S.6.3.2 | Waste collection facilities (e.g. litter bins) to be included in the design of the supporting facilities, and at regular intervals along the route. The Government Department responsible for managing the facilities will be responsible for arranging for regular collection of litter from these facilities. Separate collection bins shall be provided for aluminium cans, plastic drinks bottles and paper wastes, which will facilitate recycling of these waste streams | Waste management during operational phase | LCSD for management and maintenance of facilities FEHD for arranging regular collection of refuse | All Resting Stations and along the cycle track. Collection of refuse at regular interval | EIA, Contractual requirements |

Table A1-5 Land Contamination – Implementation Schedule of Recommended Mitigation Measures

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|--------------------|-----------|---|---|--------------------------------|--|--|
| Construction Phase | | | | | | |
| S.8.7.2 – S.8.7.3 | S.7.2.2 | Preparation of Contamination Assessment Plan (CAP), which should be submitted to EPD for endorsement, prior to investigation. Site investigation and sampling works in accordance with the approved CAP. If contamination is identified, Contamination Assessment Report (CAR) and Remediation Action Plan (RAP) shall be prepared and submitted for EPD's approval. | To formulate CAP and CAR to assess the land contamination impact | Project Proponent, Contractor | Prior to construction works within the area 5 m of the Project alignment neighbouring Sites A to F, and works area of the cycle track section along Castle Peak Road – San Tin near San Sham Road. | Guidance Note for Contaminated Land Assessment and Guidance Notes for Investigation and Remediation of Contaminated Sites of Petrol Filling Stations, Boatyards, and Car Repair/ Dismantling Workshops |
| S.8.7.5 | S.7.3.1 | The following control measures should be implemented when handling identified contaminated materials: <ul style="list-style-type: none"> ▪ General site safety shall be enforced to include basic practices such as the use of safety boots, hard hats, coveralls, gloves and eye protection; ▪ Avoid skin contact, ingestion and inhalation of excavated contaminated soils. Basic personal protective equipment should be used; ▪ Site staff and workers shall be given adequate training and instructions specific to the potential hazards, their health and safety responsibilities and safe working practice including basic personal hygiene; ▪ Measures shall be implemented to prevent non-workers from approaching the identified works areas in order to avoid exposure to contaminants. | Safety precautionary measures for identified contaminated materials | Contractors | During construction at works areas neighbouring Sites A to F and works area of the cycle track section along Castle Peak Road – San Tin near San Sham Road | Guidance Note for Contaminated Land Assessment and Guidance Notes for Investigation and Remediation of Contaminated Sites of Petrol Filling Stations, Boatyards, and Car Repair/ Dismantling Workshops |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|-------------------|-----------|---|---|--------------------------------|--|--|
| S.8.7.5 | S.7.3.1 | <p><u>Management of Contaminated Soils</u></p> <ul style="list-style-type: none"> ▪ Where appropriate, the use of bulk handling equipment should be maximised to reduce the potential contacts between excavated contaminated materials and associated workers; ▪ The plants for excavation and transportation of the material shall be cleaned prior to leaving the Site; ▪ All temporary stockpiles of the materials shall be completely covered with plastic/ tarpaulin sheets, particularly during heavy rainstorms. The stockpiling areas should be concrete-paved or lined with its perimeter constructed of a concrete bund where appropriate in order to avoid any leachate from migrating out of the area; ▪ Any vehicles transporting the material shall be suitably covered to limit potential dust emissions; ▪ Surface waters shall be diverted around any contaminated areas or stockpiles to minimize potential runoff into excavations, as runoff might increase the volume of contaminated water requiring disposal and suspended solids in the wastewater stream | Proper management of contaminated soils | Contractors | During construction at works areas neighbouring Sites A to F and works area of the cycle track section along Castle Peak Road – San Tin near San Sham Road | Guidance Note for Contaminated Land Assessment and Guidance Notes for Investigation and Remediation of Contaminated Sites of Petrol Filling Stations, Boatyards, and Car Repair/ Dismantling Workshops |
| Operational Phase | | | | | | |
| N/A | N/A | None specific | N/A | N/A | N/A | N/A |

Table A1-6 Ecological & Fisheries Impact – Implementation Schedule of Recommended Mitigation Measures

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|---------------------|-----------|---|--|--------------------------------|--|---|
| Construction Phase | | | | | | |
| S.9.11.4 | S.8.2.3 | Prior to tree felling, survey inspections should be made for their suitability for roosting bats. Once these trees have been highlighted, then appropriate checks of each tree for bats should be made prior to removal as a precautionary measure. It is more realistic to further assess the trees with potential for bat roosting at a later stage in the project, programmed at such a time that a survey can be completed in a reasonable timescale prior to felling | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor, ET | During construction | EIA, Contractual requirements |
| S.9.11.17 - 9.11.19 | S.8.2.4 | For the Kam Tin section and the Long Valley section of the Project, construction works shall be carried out during the dry season (October to March) which is considered to have no significant impact to wildlife and to avoid the breeding season of Greater Painted-snipes at Long Valley. This is also to prevent any site run-off to adjacent water channels and fishponds including those fishponds along San Tin Tsuen Road. | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor | During construction | EIA, Contractual requirements |
| S.9.11.23 | S.8.2.5 | Construction of the section in the vicinity of Mai Po Egretty would need to be completed outside of the recognised breeding season for Ardeids in Hong Kong to prevent any disturbance to the nesting birds. This breeding season is from March to August inclusive. Therefore, construction should take place between the months of <u>September to February</u> to avoid any disturbance to breeding and nesting birds | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor | During construction | EIA, Contractual requirements |
| S.9.11.25 | S.8.2.6 | Planting of tall bamboo or other vegetation could also be implemented at the corner of Mai Po Road and Castle Peak Road on the northern side to act as a screen between the cycle track and egretty. This may help to reduce any potential disturbance to breeding ardeids | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor | During construction | EIA, Contractual requirements |
| S.9.11.7 | S.8.2.6 | <i>In situ</i> compensation planting should occur at the Information Kiosk and R9, to provide continuing function of the bamboo and plantation (as well as the provision of potential roosting habitats for birds, an anticipated benefit of the mitigation planting from a previous project (Maunsell 1998). | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor | During construction | EIA, Contractual requirements |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|-----------|-----------|---|--|--------------------------------|--|---|
| S.10.5.1 | S.8.2.2 | Local narrowing of the cycle track (from 4m to 3m) shall be implemented to avoid the impact of the cycle track on the single, inactive fishpond edge just outside Mai Po Village (see Figure 10-1 of the EIA Report). | Fisheries – to minimize impact to fisheries | Contractor | During construction | EIA, Contractual requirements |
| S.10.5.4 | S.8.2.7 | Good site practice must be employed at all times, particularly in the areas close to fishponds. Practice Note for Professional Persons ProPECC PN1/94 – Construction Site Drainage shall be implemented | Fisheries – to minimize impact to fisheries | Contractor | During construction | EIA, Contractual requirements |
| S.10.5.4 | S.8.2.8 | Along Pok Wai South Road and San Tin Tsuen Roads, once the final construction sequencing is known, liaison with local residents and aquaculturists should be implemented in order to minimize temporary road blockages and to identify the best timing for works along this area | Fisheries – to minimize impact to fisheries | Contractor | During construction | EIA, Contractual requirements |
| S.10.5.3 | S.8.2.9 | During wet seasons, surface run-off from the construction sites will need to be directed into storm drains via adequately designed wastewater treatment facilities such as sand traps, silt traps and sediment settling basins. Works adjacent to the fishponds near NTMDC inside the Wetland Conservation Area (WCA) and Mai Po San Tsuen should be avoided, as far as practicable, during the wet season to avoid runoff into the fishponds | Fisheries – to minimize impact to fisheries | Contractor | During construction | EIA, Contractual requirements |
| S.9.11.27 | S.8.2.11 | The following good work practices are recommended: <ul style="list-style-type: none"> ▪ Avoid soil storage against trees; ▪ Fence off any potentially ecologically sensitive areas; ▪ Delineation of works area to prevent encroachment onto adjacent habitats; ▪ Reinstatement of habitat after works; ▪ No on-site burning of waste; ▪ Waste and refuse in appropriate receptacles; ▪ Staff training/toolbox talks for site work near Long Valley and WCA – important areas for birds therefore staff should reduce amount of noise whilst working and during breaks where possible; ▪ Regular ecological checks; and ▪ Silt/ Sediment/ Oil traps for drainage to prevent site run-off | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor | During construction | EIA, Contractual requirements |

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|-------------------|-----------|---|--|--------------------------------|--|---|
| Operational Phase | | | | | | |
| S.9.11.26 | S.8.2.10 | Implementation of signage at the Resting Stations to indicate that wildlife may be present and that noise levels and activities should be kept to a minimum could be implemented to help to reduce any potential disturbance to wildlife. | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor | During construction | EIA, Contractual requirements |
| S.9.11.26 | S.8.2.10 | At Long Valley, to mitigate against potential indirect human disturbance to Greater Painted-snipe, planting could be undertaken as appropriate along the proposed cycle track at meander 8 to act as screening. | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor | During construction | EIA, Contractual requirements |
| S.9.13.2 | S.8.3.1 | Operational Phase EM&A will comprise of an audit undertaken by the ET Leader during the first year of operation of the cycle track to ensure appropriate implementation of mitigation measures including signage, mitigation planting at Mai Po Egretty, R9 and planting for screening at meander 8 in Long Valley. | Ecological – to minimize ecological impact/ ecological enhancement works | Contractor, ET | During operation | EIA, Contractual requirements |

Table A1-7 Cultural Heritage Impact – Implementation Schedule of Recommended Mitigation Measures

| EIA Ref. | EM&A Ref. | Recommended Environmental Protection Measures/ Mitigation Measures | Objectives of the recommended measures & main concerns to address | Who to implement the measures? | Location/ Timing of implementation of Measures | What requirements or standards for the measures to achieve? |
|--------------------|-----------|--|---|--------------------------------|--|---|
| Construction Phase | | | | | | |
| S.11.5.1 | S.9.2.1 | Care should be taken during the construction stage to report any signs of possible discovery of artefacts. | Cultural heritage protection | Contractors | During the construction period | AMO |
| Operational Phase | | | | | | |
| N/A | N/A | None specific | N/A | N/A | N/A | N/A |

Table A1-8 Landscape & Visual Impact – Implementation Schedule of Recommended Mitigation Measures

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|-----------------------|-----------|--|----------|-------------------|--------------------------------------|---|-----------------------|---|---|--------------------------|---|
| | | | | | | | D | C | O | | |
| Detailed Design Phase | | | | | | | | | | | |
| Table 12-11 | CP1 | A detailed tree survey to be carried out by the IDC Consultant during the detailed design stage. The recommendations of the preliminary tree survey shall be reviewed and confirmed during the detailed survey. Should tree felling be required, tree felling application is required in accordance with ETWB TCW No. 3/2006, Tree Preservation | Site | Project Proponent | Project Proponent, IDC Consultant | EIA, Contractual requirements Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | | | During detailed design | Landscape mitigation measures |
| S.12.9.3 | CP6 | It has been agreed that the proposed landscape areas under DSD's 4215DS project which falls within the cycle track works area will be implemented by Project proponent of this Project in form of roadside amenity areas after completion of the cycle track. During the detailed design, the works programme of this Project shall be coordinated with the above-mentioned DSD project in order to avoid abortive planting works and impact on landscape resources between the interface of different public works. The proposed landscape areas under 4215DS fallen within the cycle track works area shall be incorporated in the final landscape design of this Project. | Site | Project Proponent | Project Proponent, IDC Consultant | EIA, Contractual requirements Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | | | During detailed design | Landscape mitigation measures |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|---|-----------|--|----------|-------------------|---|---|-----------------------|---|---|------------------------------------|---|
| | | | | | | | D | C | O | | |
| S.12.10.1 | OP1 | The Design Concept Drawings and Conceptual Landscape Master Plan of cycle track and associated facilities demonstrate landscape and visual mitigation strategies and design measures including integrated design approach, amenity and compensatory planting proposals and treatment of retaining structure and slopes have been recommended in the EIA. More detailed landscape and compensatory planting proposals shall be developed by IDC consultants at later stage during detailed design and construction phase of this project following the completion of the detailed Tree Survey Report and approval from relevant departments at that stage | Site | Project Proponent | Project Proponent, IDC Consultant | EIA, Contractual requirements Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | | | During detailed design | Landscape mitigation measures |
| Construction Phase Landscape and Visual Mitigation Measures | | | | | | | | | | | |
| Table 12-11 | CP1 | Preservation of Existing Vegetation | | | | | | | | | |
| | CP1.1 | To retain trees, which have high amenity or ecology value and contribute most to the landscape and visual amenity of the site and its immediate environs. | Site | Project Proponent | Project Landscape Architect / Contractor, Project Proponent | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | | | Throughout design phase | To minimize the disturbance to the existing landscape resources. |
| | CP1.2 | Creation of precautionary area around trees to be retained equal to half of the trees canopy diameter. Precautionary area to be fenced. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | | ✓ | | Before Construction phase Commence | To ensure the success of the tree preservation proposals. |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|----------|-----------|--|----------|-------------------|-----------------------------------|--|-----------------------|---|---|-------------------------------|---|
| | | | | | | | D | C | O | | |
| | CP1.3 | Prohibition of the storage of materials including fuel, the movement of construction vehicles, and the refuelling and washing of equipment including concrete mixers within the precautionary area. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | | ✓ | | Throughout construction phase | To ensure the success of the tree preservation proposals. |
| | CP1.4 | Phased segmental root pruning for trees to be retained and transplanted over a suitable period (determined by species and size) prior to lifting or site formation works which affect the existing rootball of trees identified for retention. The extent of the pruning will be based on the size and the species of the tree in each case. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | | ✓ | | Throughout construction phase | To ensure the success of the tree preservation proposals. |
| | CP1.5 | Pruning of the branches of existing trees identified for transplantation and retention to be based on the principle of crown thinning maintaining their form and amenity value. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | | ✓ | | Throughout construction phase | To ensure the success of the tree preservation proposals. |
| | CP1.6 | The watering of existing vegetation particularly during periods of excavation when the water table beneath the existing vegetation is lowered. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | | ✓ | | Throughout construction phase | To ensure the success of the tree preservation proposals. |
| | CP1.7 | The rectification and repair of damaged vegetation following the construction phase to it's original condition prior to the commencement of the works or replacement using specimens of the same species, size and form where appropriate to the design | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | | ✓ | | Throughout construction phase | To ensure the success of the tree preservation proposals. |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|-------------|-----------|---|----------|-------------------|---|--|-----------------------|---|---|---|---|
| | | | | | | | D | C | O | | |
| | | intention of the area affected | | | | | | | | | |
| | CP1.8 | All works affecting the trees identified for retention and transplantation will be carefully monitored. This includes the key stages in the preparation of the trees, the implementation of protection measures and health monitoring through out the construction period | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | | ✓ | | Throughout construction phase | To ensure the success of the tree preservation proposals. |
| | CP1.9 | Detailed landscape and tree preservation proposals will be submitted to the relevant government departments for approval under the lease conditions and in accordance with ETWB TCW No. 2/2004 and WBTC No. 14/2002. | Site | Project Proponent | Project Proponent, Project Landscape Architect / NA | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | | | Throughout design phase | To ensure the tree preservation and planting proposals are integrated with the existing landscape context and that the landscape resources are preserved where appropriate. |
| | CP2.0 | The tree preservation works should be implemented by approved Landscape Contractors and inspected and approved on site by a qualified Landscape Architect. A tree protection specification would be included within the contract documents. | Site | Project Proponent | Landscape Architect, Project Proponent / NA | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | ✓ | | Throughout design and construction phases | To ensure the tree preservation and planting proposals are integrated with the existing landscape context and that the landscape resources are preserved where appropriate. |
| Table 12-11 | CP2 | Preservation of Existing Topsoil | | | | | | | | | |
| | CP2.1 | Topsoil disturbed during the construction phase should be tested using a standard soil testing methodology and where it is found to be worthy of retention stored for re-use. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM | | ✓ | | Throughout construction phase | To provide a viable growing medium suited to the existing conditions and reduce the need for the importation of topsoil. |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|-------------|-----------|---|----------|-------------------|-----------------------------------|----------------------------------|-----------------------|---|---|--------------------------------|--|
| | | | | | | | D | C | O | | |
| | CP2.2 | The soil will be stockpiled to a maximum height of 2m and will be either temporarily vegetated with hydroseeded grass during construction or covered with a waterproof covering to prevent erosion. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM | | ✓ | | Throughout construction phase | To provide a viable growing medium suited to the existing conditions and reduce the need for the importation of topsoil. |
| | CP2.3 | The stockpile should be turned over on a regular basis to avoid acidification and the degradation of the organic material, and reused after completion. Alternatively, if this is not practicable, it should be considered for use elsewhere, including other projects. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM | | ✓ | | Throughout construction phase | To provide a viable growing medium suited to the existing conditions and reduce the need for the importation of topsoil. |
| Table 12-11 | CP3 | Works Area and Temporary Works Areas | | | | | | | | | |
| | CP3.1 | Where appropriate to the final design the landscape of these works areas should be restored following the completion of the construction phase. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM | | ✓ | | Through out construction phase | To minimize the disturbance to existing landscape resources and change of visual amenity. |
| | CP3.2 | Construction site controls should be enforced including the storage of materials, the location and appearance of site accommodation and the careful design of site lighting to prevent light spillage. | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM | | ✓ | | Through out construction phase | To minimize the disturbance to existing landscape resources and change of visual amenity. |
| | CP3.3 | Screen the works area during the construction phase through the use of decorative hoarding along the site boundary facing adjacent VSRs | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM | | ✓ | | Through out construction phase | To minimize the disturbance to existing landscape resources and change of visual amenity. |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|-------------|-----------|--|----------|-------------------|---|--|-----------------------|---|---|--|--|
| | | | | | | | D | C | O | | |
| Table 12-11 | CP4 | Mitigation Planting | | | | | | | | | |
| | CP4.1 | Replanting of disturbed vegetation should be undertaken at the earliest possible stage of the construction phase | Site | Project Proponent | Contractor / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | | ✓ | | After the site formation and on completion of planting area. | To minimize the disturbance to existing landscape resources and minimize the impacts on the visual amenity of the area. |
| | CP4.2 | Use of native plant species predominantly in the planting design for the buffer areas. | Site | Project Proponent | Project Landscape Architect/ NA | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | ✓ | | After the site formation and on completion of planting area. | To enhance the local landscape and ecological value. |
| | CP4.3 | The tree planting works should be implemented by approved Landscape Contractors and inspected and approved on site by a qualified Landscape Architect. A tree planting specification would be included within the contract documents. | Site | Project Proponent | Landscape Architect, Project Proponent / NA | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | ✓ | | Throughout design and construction phases | To ensure the tree preservation and planting proposals are integrated with the existing landscape context and that valuable landscape resources are preserved where appropriate to the final design. |
| Table 12-11 | CP5 | Transplantation of Existing Trees | | | | | | | | | |
| | CP5.1 | The tree transplanting works should be implemented by approved Landscape Contractors and inspected and approved on site by a qualified Landscape Architect. A tree protection / transplanting specification would be included within the contract documents. | Site | Project Proponent | Project Proponent / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | ✓ | | Throughout design and construction phases | To ensure the tree preservation and planting proposals are integrated with the existing landscape context and that valuable landscape resources are preserved where appropriate to the final design. |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|--|-----------|---|----------|-------------------|------------------------------------|--|-----------------------|---|---|---|--|
| | | | | | | | D | C | O | | |
| | CP5.2 | The implementation program should reserve enough time for advance tree transplanting preparation. | Site | Project Proponent | Project Proponent / Contractor | Annex 10 and Annex 18 of EIAO-TM, ETWB TCW No. 3/2006 & WBTC No. 14/2002 | ✓ | ✓ | | Throughout design and construction phases | To ensure the tree preservation and planting proposals are integrated with the existing landscape context and that valuable landscape resources are preserved where appropriate to the final design. |
| Operational Phase Landscape and Visual Mitigation Measures | | | | | | | | | | | |
| Table 12-12 | OP1 | Design of Cycle Track and Associated Facilities | | | | | | | | | |
| | OP1.1 | Where possible integrate the alignment, as far as technically feasible, with existing built structures. Select responsive The locations for the associated facilities away from landscape and visually sensitive areas. | Site | Project Proponent | Project Engineer and Architect/ NA | Annex 10 and Annex 18 of EIAO-TM and BD | ✓ | | | Throughout Design phase | To ensure the proposals are integrated with the existing landscape and visual context, and avoid cluster effect. |
| | OP1.2 | Where possible adopt a simple building design and building height profile, single-storey (lower than the adjacent village houses), responding to the village houses in the context. | Site | Project Proponent | Project Engineer and Architect/ NA | Annex 10 and Annex 18 of EIAO-TM and BD | ✓ | | | Throughout Design phase | To ensure the proposals are integrated with the existing landscape and visual context, and avoid cluster effect. |
| | OP1.3 | Use of natural materials such as wooden framing or sustainable materials such as recycle plastic for built structure. | Site | Project Proponent | Project Engineer and Architect/ NA | Annex 10 and Annex 18 of EIAO-TM and BD | ✓ | | | Throughout Design phase | Responsive building façade treatment to reduce the apparent visual mass of the facilities and reduce the glare effect from the reflection of sunlight. |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|-------------|-----------|---|----------|-------------------|---|--|-----------------------|---|---|-----------------------------|--|
| | | | | | | | D | C | O | | |
| | OP1.4 | Use of natural tones with non-reflective finishes on the outward facing building facades to reduce glare effect. Sustainable material such as recycle plastic shall be considered. | Site | Project Proponent | Project Engineer and Architect/ NA | Annex 10 and Annex 18 of EIAO-TM, HKPSG and BD | ✓ | | | Throughout Design phase | To reduce the nighttime glare effect to the surrounding environs. |
| | OP1.5 | Formulate lighting operation management programme to minimize potential light spillage and glare impacts. | Site | Project Proponent | HyD and ArchSD/ HyD and ArchSD | Annex 10 and Annex 18 of EIAO-TM | | | ✓ | Through out Operation phase | To reduce the nighttime glare effect to the surrounding environs. |
| Table 12-12 | OP2 | Roadside and Amenity Planting | | | | | | | | | |
| | OP2.1 | Utilise large ornamental trees with high canopy and thin foliage to allow some through views from the adjacent neighbourhood and give accent to the existing road planting and wooded areas with the advantage of creating a more coherent landscape framework whilst native species will utilise on sloping area improving the ecological connectivity between existing woodland habitats. | Site | Project Proponent | Project Landscape Architect / AFCD and LCSD | Annex 10 and Annex 18 of EIAO-TM, HKPSG and BD | ✓ | | ✓ | Through out Design phase | Provide a linkage with the existing roadside and woodland planting areas creating a more coherent landscape framework. |
| | OP2.2 | Large Feature Trees will utilise within the resting station and education centre or along the cycle tracks where space allows | Site | Project Proponent | Project Landscape Architect / AFCD and LCSD | Annex 10 and Annex 18 of EIAO-TM, HKPSG & BD | ✓ | | ✓ | Through out Design phase | Conserve and enhance the landscape interest. |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|-------------|-----------|--|----------|-------------------|---|--|-----------------------|---|---|--------------------------|--|
| | | | | | | | D | C | O | | |
| Table 12-12 | OP3 | Compensatory Planting Proposals | | | | | | | | | |
| | OP3.1 | Utilise ornamental species along the track and within the resting stations and education whilst species native to Hong Kong will be added the roadside planting along cycle track or on sloping area | Site | Project Proponent | Project Landscape Architect / AFCD and LCSD | Annex 10 and Annex 18 of EIAO-TM, HKPSG and BD | ✓ | | ✓ | Through out Design phase | The planting proposal seeks to compensate for the predicted tree loss resulting from the construction of the proposed works, visually integrate the proposals within its existing landscape framework and provide an improved visual amenity for future residents. |
| | OP3.2 | A qualified or registered landscape architect will be involved in the design, construction supervision and monitoring, and maintenance period to oversee the implementation of the recommended landscape and visual mitigation measures including the tree preservation and landscape works on site. | Site | Project Proponent | Project Proponent / NA | Annex 10 and Annex 18 of EIAO-TM, HKPSG and BD | ✓ | | | Through out Design phase | The planting proposal seeks to compensate for the predicted tree loss resulting from the construction of the proposed works, visually integrate the proposals within its existing landscape framework and provide an improved visual amenity for future users. |

| EIA Ref. | Mit. Code | Recommended Mitigation Measures | Location | Funding | Implementation/ Maintenance Agent | Relevant Standard or Requirement | Implementation Stages | | | Timing of Implementation | Objectives of the Recommended Measure and Main Concern to address |
|-------------|-----------|---|----------|-------------------|------------------------------------|--|-----------------------|---|---|--------------------------|--|
| | | | | | | | D | C | O | | |
| Table 12-12 | OP4 | Treatment of Retaining Wall and Slopes | | | | | | | | | |
| | OP4.1 | Use of soft landscape works including tree and shrub planting to give man-made slopes a more natural appearance blending into the woodland setting for the development | Site | Project Proponent | Project Landscape Architect / AFCD | Annex 10 and Annex 18 of EIAO-TM, HKPSG and BD GEO Publication No. 1/2000 "Technical Guidelines on Landscape Treatment and Bio-engineering for Man-made Slopes and Retaining Walls" | ✓ | | | Through out Design phase | The design seeks to visually integrate the engineered slope feature within the rural and riverside landscapes. |
| | OP4.2 | Utilise whip sized planting on the face of soil cut slopes and at the crest and toe of the slope, and within berm planters these smaller, younger plants adapt to their new growing conditions more quickly than larger sized stock and establish a naturalistic effect more rapidly. | Site | Project Proponent | Project Landscape Architect/ AFCD | Annex 10 and Annex 18 of EIAO-TM, HKPSG and BD GEO Publication No. 1/2000 "Technical Guidelines on Landscape Treatment and Bio-engineering for Man-made Slopes and Retaining Walls" | ✓ | | ✓ | Through out Design phase | The planting proposal seeks to integrate the engineered slope feature within the rural and riverside landscapes. |

Legend: D – Design, C – Construction, O - Operation

Note: BD– Building Ordinance

ETWB TCW – Environmental and Transport Works Bureau Technical Circular

HKPSG – Hong Kong Planning Standards and Guidelines

EIAO-TM – Technical Memorandum on Environmental Impact Assessment Process

TPO – Town Planning Ordinance

WBTC - Works Bureau Technical Circulars
