Maeda - CREC - SELI Joint Venture







Contract No. DC/2007/12 – Design and Construction of Tsuen Wan Drainage Tunnel

Quarterly EM&A Report

(July - September 2008)

October 2008

Report no: EB000364R0123

Hyder Consulting Limited

Company Number 126012 47th Floor, Hopewell Centre, 183 Queens Road East, Wanchai, Hong Kong

Tel: +852 2911 2233 Fax: +852 2805 5028

hyder.hk@hyderconsulting.com



Consulting

Maeda - CREC - SELI Joint Venture







Contract No. DC/2007/12 – Design and Construction of Tsuen Wan Drainage Tunnel

Quarterly EM&A Report

(July - September 2008)

Hydei

Author:

Carman CHUNG / Winnie MA

Checker:

Antony WONG

Approver:

Alexi BHANJA

Report no:

EB000364R0123

Data

October 2008

This report has been prepared for Maeda - CREC - SELI Joint Venture in accordance with the terms and conditions of appointment for Environmental Monitoring and Audit Manual dated 18 December 2007. Hyder Consulting Ltd (COI Number 126012) cannot accept any responsibility for any use of or reliance on the contents of this report by any third party.

Certified by Environmental Team Leader Antony WONG Verified by Independent Environmental Checker David YEUNG

Consulting

Contents

Exe	cutive \$	Summary	/	5
1				
2	Proj	Project Information		
	2.1	Project	Organization and Management Structure	7
	2.2	Constru	uction Progress	7
	2.3	Mitigatio	on Measures	8
3	EM8	A Requi	rement	8
	3.1	Genera	ıl	8
	3.2	EM&A	on Air Quality, Noise and Water Quality	8
		3.2.1	Monitoring Parameters	8
		3.2.2	Monitoring Locations	
		3.2.3	Performance Limits (AL Levels)	10
		3.2.4	Monitoring Result	11
4	Qua	rterly Sui	mmary, Environmental Condition and Non-Compliance R	lecords 15
	4.1	Summa	ary of Waste Disposal Records	15
	4.2	Weathe	er Conditions	15
	4.3	Summa	ary of Exceedances	15
5	Com	plaint		16
6		•	Notification of Summons, Successful Prosecutions and	
7	Com	nments, R	Recommendations and Conclusion	16

List of Tables

Table 3-1	Frequency of Air Quality; Noise and Water Quality Monitoring
Table 3-2	Air Quality Monitoring Locations
Table 3-3	Noise Monitoring Locations
Table 3-4	Water Quality Monitoring Locations
Table 3-5	Action & Limit Levels for Air Quality
Table 3-6	Action & Limit Levels for Noise
Table 3-7	Action/Limit Levels for Water Quality
Table 3-8	Summary of Air Quality Monitoring Results
Table 3-9	Summary of Impact Noise Monitoring Results
Table 3-10	Summary of Impact Water Quality Monitoring Results
Table 4-1	Waste Generated from July to September 2008
Table 4-2	Summary of Project- related Exceedances
Table 5-1	Cumulative Statistic of Environmental Complaints
Table 6-1	Cumulative Statistics of notification of summons and successful prosecutions

Appendices

Appendix A

Site Map and Work Area

Appendix B

Organization Chart

Appendix C

Work Programme

Appendix D

Implementation Status of Environmental Mitigation Measures

Appendix E

Monitoring Locations

Appendix F

Monitoring Results

Appendix G

Interim Notifications of Environmental Quality Limits Exceedances



Executive Summary

- 1. This quarterly EM&A summary report under the Main Contract for the Design and Construction of Tsuen Wan Drainage Tunnel (hereafter referred to as the "Project") to Maeda-CREC-SELI Joint Venture (MCSJV), which summarises the findings of environmental impact monitoring works during the period from July to September 2008.
- 2. Noise monitoring was performed at five monitoring stations (NSR1, NSR3, NSR6, NSR8 and NSR9). Air quality monitoring was carried out at four monitoring stations (ASR1, ASR3, ASR8 and ASR9). Water quality monitoring was carried out at three monitoring stations (Intake I-1, Intake I-2 and Intake I-3). Noise level was measured in terms of L_{eq}, L₁₀ and L₉₀ (30min). Air quality was measured in terms of 1-hour Total Suspended Particulates (TSP). Water quality was measured in terms of Temperature, pH, Dissolved Oxygen (DO), Turbidity (Tby) and Suspended Solid (SS).
- 3. Details of all monitoring stations are summarized in the below table.

Type of Monitoring	Monitoring Station ID	Name of Premises	Status of Monitoring Works during the Reporting Period
Air Quality	ASR1	Sik Sik Yuen Ho Fung College	Ongoing
Monitoring	ASR3	Hong Hoi Chee Hong Temple	Ongoing
	ASR8	Beach Tower (Long Beach Gardens)	Ongoing
	ASR9	Greenview Terrace (Block 1)	Ongoing
Noise Monitoring	NSR1	Sik Sik Yuen Ho Fung College	Ongoing
	NSR3	Hong Hoi Chee Hong Temple	Ongoing
	NSR6	Squatters	Ongoing
	NSR8	Beach Tower (Long Beach Gardens)	Ongoing
	NSR9	Greenview Terrace (Block 1)	Ongoing
Water Quality Monitoring	I-1	Intake I-1	Ongoing
INIONITOTING	I-2	Intake I-2	Ongoing
	I-3	Intake I-3	Ongoing
	0-1	Outfall O-1	Not yet commenced until construction of rip rap is in place.

- 4. The major construction activities undertaken by the Contractor during the period from July to September 2008 include site clearance, hoarding & fencing erection, tree survey & transplanting, slope stabilization, site office formation, pre-construction survey, soil nailing, relocation of verified boulder, formation of access road and pre-bore H-piling.
- 5. No construction activities were carried out during the restricted hours during the reporting period.
- 6. No exceedance of Action/Limit Levels for air quality, noise and water quality monitoring related to Project activities were recorded during the reporting period. The below table summarizes the exceedances of air quality, noise and water quality in the reporting period.



	Action Level Exceedance	Limit Level Exceedance
Air	Nil	Nil
Noise	Nil	Nil
DO	Nil	Nil
Turbidity	One recorded at I-2 on 11 July	■ Three recorded at I-1 on 2 and 4 July and 5 September
		■ Four recorded at I-3 on 8, 11, 16 and 21 July
SS	One record at I-2 on 11 August	■ Three recorded at I-1 on 30 Jul, 1 and 5 September
		 Three recorded at I-2 on 13 August, 5 and 25 September
		■ Three recorded at I-3 on 11 and 16 July and 13 August

Note: None of these exceedances are related to project's activities

7. Waste figures during the reporting period are summarized in the below table.

Status of waste management	
Inert C&D Material Disposed of to Public Fill at Tuen Mun (m³)	154
Inert C&D Material Reused in the Contract (m³)	445
Metals Generated (kg)	300
Paper / Cardboard Packaging (kg)	750
Plastics (kg)	0
Chemical Waste (kg)	0
General Waste Disposed of to NENT Landfill (m³)	91

- 8. No environmental complaint was received in the reporting quarter.
- 9. No Notification of Summons was received since the commencement of the Project.



1 Introduction

- 1.1.1 The Drainage Services Department (DSD) proposes to construct a tunnel of an internal diameter of 6.5m and length 5.13km, with the purpose to alleviate the flooding risk in Tsuen Wan and Kwai Chung.
- 1.1.2 This project is a Designated Project under Schedule 2 Part I Category Q, of the Environmental Impact Assessment Ordinance (EIAO) as part of the proposed Tsuen Wan Drainage Tunnel (TWDT) passes underneath the existing Tai Mo Shan Country Park. An Environmental Impact Assessment (EIA) Study has therefore been undertaken to provide information on the nature and extent of environmental impacts arising from the construction and operation of the proposed designed project and related activities taking place concurrently. From the EIA the recommendations for monitoring contained herein, are made.
- 1.1.3 The Maeda CREC SELI Joint Venture (MCSJV) was awarded by DSD with the Contract Design and Construction of Tsuen Wan Drainage Tunnel.
- 1.1.4 Hyder was commissioned by the MCSJV as the ET to implement an EM&A program in accordance with the EM&A Manual. The proposed tunnel section flows from the junction of Shing Mun Road and Wo Yi Hop Road and discharges to south of Yau Kom Tau underneath Castle Peak Road as shown in Appendix A.
- 1.1.5 The construction works of the Project commenced on January 2008. This is the second quarterly EM&A report summarising the impact monitoring results and audit findings of the EM&A program during the reporting period in July September 2008.

2 Project Information

2.1 Project Organization and Management Structure

2.1.1 The organization chart and lines of communication with respect to the on-site environmental management are shown in Appendix B.

2.2 Construction Progress

- 2.2.1 It is anticipated that the overall project programme from the detail design to completion of all civil works shall take approximately 54 months. The construction programme is presented in Appendix C.
- 2.2.2 The major construction activities undertaken in the reporting quarter are:
 - Site clearance;

- Hoarding & fencing erection;
- Tree survey & transplanting;



- Slope stabilization;
- Site office formation;
- Pre-construction survey;
- Soil nailing;
- Relocation of verified boulder;
- Formation of access road; and
- Pre-bore H-piling

2.3 Mitigation Measures

2.2.3 The environmental mitigation measures that have been implemented and their status are given in Appendix D.

3 EM&A Requirement

3.1 General

Sep08\EB000364R0123.doc

3.1.1 The EM&A requirements are stipulated in the EM&A Manual. The principal purposes of the EM&A program are to assess the compliance with applicable environmental legislation and associated regulations; to ensure the implementation of mitigation measures specified in the EM&A Manual; and to identify any remedial works necessary for redressing any unacceptable or unanticipated environmental impacts.

3.2 EM&A on Air Quality; Noise and Water Quality

Monitoring Parameters

- 3.2.1 The air quality; noise and water quality frequencies and parameters are shown in Table 3-1.
- 3.2.2 During the reporting quarter, one scheduled water quality monitoring in the 2nd week of July 2008 (from 7 July to 13 July) and one scheduled water quality monitoring in the 4th week of August 2008 (from 18 August to 24 August) were cancelled due to unfavourable weather conditions. Details can be referred to monthly EM&A reports accordingly.



Type of Monitoring	Monitoring Station ID	Parameter	Frequency
Air Quality Monitoring	ASR1; ASR3; ASR8 and ASR9	1-hour TSP	Once every 6-day
Noise Monitoring	NSR1; NSR3; NSR6; NSR8 and NSR9	Leq (30 min.)	Once every week
Water Quality Monitoring	I-1; I-1-C; I-2; I-2-C; I-3; I-3-C	DO (mg/l)	Three days per week
		SS (mg/l)	
		Turbidity (NTU)	
		рН	
		Temperature (°C)	

Table 3-1 Frequency of Air Quality; Noise and Water Quality Monitoring

Monitoring Locations

The monitoring locations for air quality; noise and water quality are shown in Tables 3-2; 3-3; 3-4 and Appendix E.

Monitoring Station ID	Name of Premises	Floor Level
ASR1	Sik Sik Yuen Ho Fung College	G/F
ASR3	Hong Hoi Chee Hong Temple	Podium
ASR8	Beach Tower (Long Beach Gardens)	G/F
ASR9	Greenview Terrace (Block 1)	G/F

Table 3-2 Air Quality Monitoring Locations

Monitoring Station ID	Name of Premises	Floor Level
NSR1	Sik Sik Yuen Ho Fung College	G/F
NSR3	Hong Hoi Chee Hong Temple	Podium
NSR6	Squatters	G/F
NSR8	Beach Tower (Long Beach Gardens)	G/F
NSR9	Greenview Terrace (Block 1)	G/F

Table 3-3 Noise Monitoring Locations



Monitoring Station ID	Name of Premises
I-1	Intake I-1
I-1-C	Control of Intake I-1
I-2	Intake I-2
I-2-C	Control of Intake I-2
I-3	Intake I-3
I-3-C	Control of Intake I-3
O-1 (FT)*	Outfall 1During Flood Tide
O-1 (ET)*	Outfall 1During Ebb Tide
O-1-C (FT)*#	Control of Outfall O-1 During Flood Tide
O-1-C (ET)*#	Control of Outfall O-1 During Ebb Tide

Note: *Water quality monitoring will be undertaken when the construction of rip rap is in placed.

#Note that there are two control stations for Outfall O-1; one for sampling during flood tide and one for sampling during ebb tide. Only one of those control stations for Outfall O-1 shall be sampled during each sampling. Control station to be sampled will be determined base on the tidal information provided by the Hong Kong Observatory.

Table 3-4 Water Quality Monitoring Locations

Performance Limits (AL Levels)

3.2.4 In accordance with the EM&A Manual; the appropriate Action and Limit Levels for Air Quality; Noise and Water Quality were established and are presented in Tables 3-5; 3-6 and 3.7. Should non-compliance of the air quality; noise and water quality criteria occur; actions in accordance with the Event / Action Plan stipulated in contract specific EM&A Manual should be carried out.

Station	1-hr TSP Le	evel in µg/m³
Station	Action Level	Limit Level
ASR1	307	500
ASR3	327	500
ASR8	337	500
ASR9	329	500

Table 3-5 Action & Limit Levels for Air Quality

Time Period	Action	Limit
0700 – 1900 hrs on normal weekdays		75 dB(A)*
0700 – 2300 hrs on holidays; and	When one documented complaint	70 dB(A)
1900 – 2300 hrs on all other days	is received	
2300 – 0700 hrs of next day		55 dB(A)

^{*} For educational establishments the limit level shall be 70dB(A) and reduced to 65dB(A) during examination periods between 0700-1900 hrs on normal weekdays.

Table 3-6 Action & Limit Levels for Noise



Parameters	Action	Limit
DO in mg/l (Surface; Middle & Bottom)	Surface & Middle 5%-ile of baseline data for surface and middle layer. Bottom 5%-ile of baseline data for bottom	Surface & Middle 4mg/l except 5mg/l for FCZ or 1%-ile of baseline data for surface and middle layer Bottom 2mg/l or 1%-ile of baseline data for
SS in mg/l (Depth-averaged)	95%-ile of baseline data or 120% of upstream control station's SS at the same tide of the same day	bottom layer 99%-ile of baseline or 130% of upstream control station's SS at the same tide of the same day and specific sensitive receiver water quality requirements (e.g. required suspended solids levels for concerned sea water intakes)
Turbidity (Tby) in NTU (Depth-averaged)	95%-ile of baseline data or 120% of upstream control station's Tby at the same tide of the same day	99%-ile of baseline or 130% of upstream control station's Tby at the same tide of the same day

Notes:

- For DO; non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
- For SS and Tby; non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
- All the figures given in the table are used for reference only and the EPD may amend the figures whenever it
 is considered as necessary.

Table 3-7 Action/Limit Levels for Water Quality

Monitoring Result

3.2.5 A summary of air quality monitoring results is presented in Table 3-8 and Appendix F. No exceedance of Action and Limit Levels was recorded during the reporting period.

Monitoring Station		1-hour TSP	(μg/m³)	Action Level	Limit Level
Otation		Range)	(μg/m³)	(μg/m³)
ASR1	27	-	175	307	500
ASR3	30	-	149	327	500
ASR8	16	-	138	337	500
ASR9	15	-	114	329	500

Italic indicates the exceedances of Action Levels **Bold** indicates the exceedances of Limit Levels

Table 3-8 Summary of Air Quality Monitoring Results

3.2.6 All measured noise monitoring levels were complying with the Action and Limit Levels in the reporting period. A summary of noise monitoring results is presented in Table 3-9 and Appendix F.



Monitoring Station	Le	q (30mins) dE	B(A)	Limit Level
		Range		dB(A)
NSR1	59	-	66	70
NSR3	62	-	68	75
NSR6	58	-	64	75
NSR8	57	-	67	75
NSR9	56	-	65	75

Bold indicates the exceedances of Limit Levels

Table 3-9 Summary of Impact Noise Monitoring Results

- 3.2.7 A summary of water quality monitoring results is presented in Table 3-10 and Appendix F.
- 3.2.8 During July 2008, two exceedances of Control Limit Levels of turbidity were recorded at I-1 on 2, 4, one exceedance of Control Limit Level of SS at I-1 on 30 July and two exceedances of Control Limit Levels of SS were recorded at I-3 on 11 and 16 July. No direct disturbance or no construction activities were observed during the mentioned monitoring dates and the measured results were well below Baseline Action & Limit Levels. Therefore, those exceedances are considered to be non project-related.
- 3.2.9 Exceedance of Action Level of turbidity was recorded at I-2 on 11 July and exceedance of Limit Level of turbidity was recorded at I-3 on 8, 11, 16 and 21 July. The measured level at impact stations were similar to the control stations. As such, the exceedance was likely contributed by natural variation rather than project construction activities.
- 3.2.10 During August 2008, two exceedances of Control Limit Levels of SS (130% higher than control stations) were recorded at I-2 and I-3 on 13 August and one exceedance of Control Action Levels of SS (120% higher than control station) was recorded at I-2 on 11 August. The monitoring results of SS at I-2 and I-3 on 11 and 13 August were well below Baseline Action & Limit Levels. Levelling of piling platform and site tidying & cleaning and removal of dead trees were observed undertaken on the mentioned monitoring dates. No action is taken as there is no evidence to show the exceedance is project related.
- 3.2.11 During September 2008, two exceedances of Control Limit Levels of SS (130% higher than control stations) were recorded at I-1 on 1 September and I-2 on 25 September respectively. The measured levels at the impact stations were well below both Baseline Action & Limit Levels and no direct disturbance was observed contributed by the project construction activities. As such, no action is taken as there is no evidence to show the above exceedances are project related and no exceedance was recorded in consecutive measurements.



- 3.2.12 Limit Level Exceedance of SS and turbidity were recorded at I-1 on 5 September. In accordance with the site observation, no construction work of this project was undertaken during measurement, muddy runoff was observed from another CEDD's construction site and the runoff discharged to the upstream of the impact monitoring station I-1. As such, no action was considered to be necessary as the above exceedance was likely caused by mentioned runoff and are not project related.
- 3.2.13 Limit Level Exceedance of SS was recorded on 5 September at I-2. Regarding site observation, mobilization of geological investigation plant was observed on site during the monitoring. The exceedance may be caused by pipe leakage of an air compressor of another project (GE/2006/17). No exceedance was recorded in the consecutive monitoring measurement.



Monitoring	Temperature	DO	(mg/L)	рН	Turbio	lity (NTU)	Suspende	d Solid (mg/L)
Station	Range	Range	Action / Limit Level	Range	Range	Action / Limit Level	Range	Action / Limit Level
I-1	24.45 - 29.00	4.87 - 5.91	3.42/3.34	7.15 - 7.91	2.47 - 18.95	9.75 / 12.47	0.70 - 22.60	8.85/10.17
I-1-C	24.65 - 29.30	4.94 - 5.86	-	7.23 - 7.93	2.66 - 23.75	-	1.00 - 11.70	-
I-2	23.90 - 28.70	4.69 - 5.86	3.66 / 3.63	7.29 - 7.90	2.10 - 6.90	6.63 / 6.99	0.80 - 6.50	7.68/8.34
I-2-C	23.60 - 29.00	4.68 - 5.87	-	7.30 - 7.92	2.11 - 6.85	-	0.20 - 6.00	-
I-3	24.85 - 30.10	4.95 - 6.62	3.65 / 3.51	7.31 - 8.03	2.07 - 6.46	3.99/4.18	0.20 - 4.00	6.13/7.23
I-3-C	24.90 - 29.00	5.03 - 6.38	-	7.27 - 8.13	2.13 - 6.62	-	0.15 - 3.50	-

Note: Impact monitoring was commenced from May 2008 onward.

The Action and Limit Levels were considered not applicable to control stations since end of June 2008.

Italic indicates the exceedances of Action Levels

Bold indicates the exceedances of Limit Levels

Table 3-10 Summary of Impact Water Quality Monitoring Results



4 Quarterly Summary; Environmental Condition and Non-Compliance Records

4.1 Summary of Waste Disposal Records

4.1.1 According to the information provided by the Contractor; the quantities of C&D materials in the reporting period are summarized in Table 4-1.

Status of Waste Management	July 2008	August 2008	September 2008
Inert C&D Material Disposed of to Public Fill at Tuen Mun (m³)	154.1	Nil	Nil
Inert C&D Material Reused in other Contract (m³)	Nil	445	Nil
Metals Generated (kg)	Nil	Nil	300
Paper / Cardboard Packaging (kg)	120	180	450
Plastics (kg)	Nil	Nil	Nil
Chemical Waste (kg)	Nil	Nil	Nil
General Waste Disposed of to NENT Landfill (m³)	56.1	18.8*	15.6

^{*} As confirmed by the Contractor, the total amount of disposed general waste to NENT Lanfill is 18.8m3 instead of 56.1m3.

Table 4-1 Waste Generated from July to September 2008

4.2 Weather Conditions

4.2.1 The weather conditions during the period from July to September 2008 were mainly cloudy; inclement rainy weather and occasional sunshine.

4.3 Summary of Project-Related Exceedances

4.3.1 Summary of exceedance results are summarized in Table 4-2. For the exceedances that are considered to be non-related to the construction activities; please refer to the monthly EM&A reports separately. Appendix G shows the Interim Notifications of Environmental Quality Limits Exceedances recorded in the reporting period.



Environmental Monitoring	Total No. of Measurement	Action Level Exceedance	% of Action Level Exceedance	Limit Level Exceedance	% of Limit Level Exceedance
Air Quality	191	0	0	0	0
Noise*	65	0	0	0	0
Water	222	0	0	0	0

^{*}A total of 20 noise monitoring was undertaken in August 2008.

Table 4-2 Summary of Project- related Exceedances

5 Complaint

5.1.1 No complaint was received during the reporting period. Cumulative statistics of environmental complaints are shown in Table 5-1.

Complaints Received in the Reporting Period	Cumulative Number of Complaints
0	0

Table 5-1 Cumulative Statistic of Environmental Complaints

6 Summary of Notification of Summons; Successful Prosecutions and Corrective Actions

- 6.1.1 No summons and successful prosecution was received during the reporting period.
- 6.1.2 Cumulative statistics of Notification of Summon; Successful Prosecutions and Convictions are shown in Table 6-1.


Notificatio	n of Summons	Successf	ul Prosecution
July - September 08	Cumulative	July - September 08	Cumulative
0	0	0	0

Table 6-1 Cumulative Statistics of notification of summons and successful prosecutions

7 Comments; Recommendations and Conclusion

- 7.1.1 During the reporting period; exceedances of water quality monitoring were recorded. However none of these exceedances were related to Project's construction activities.
- 7.1.2 No environmental complaint was received during the reporting period.
- 7.1.3 No Notification of Summons has been received since the commencement of the Project.








Appendix A


Site Map and Work Area

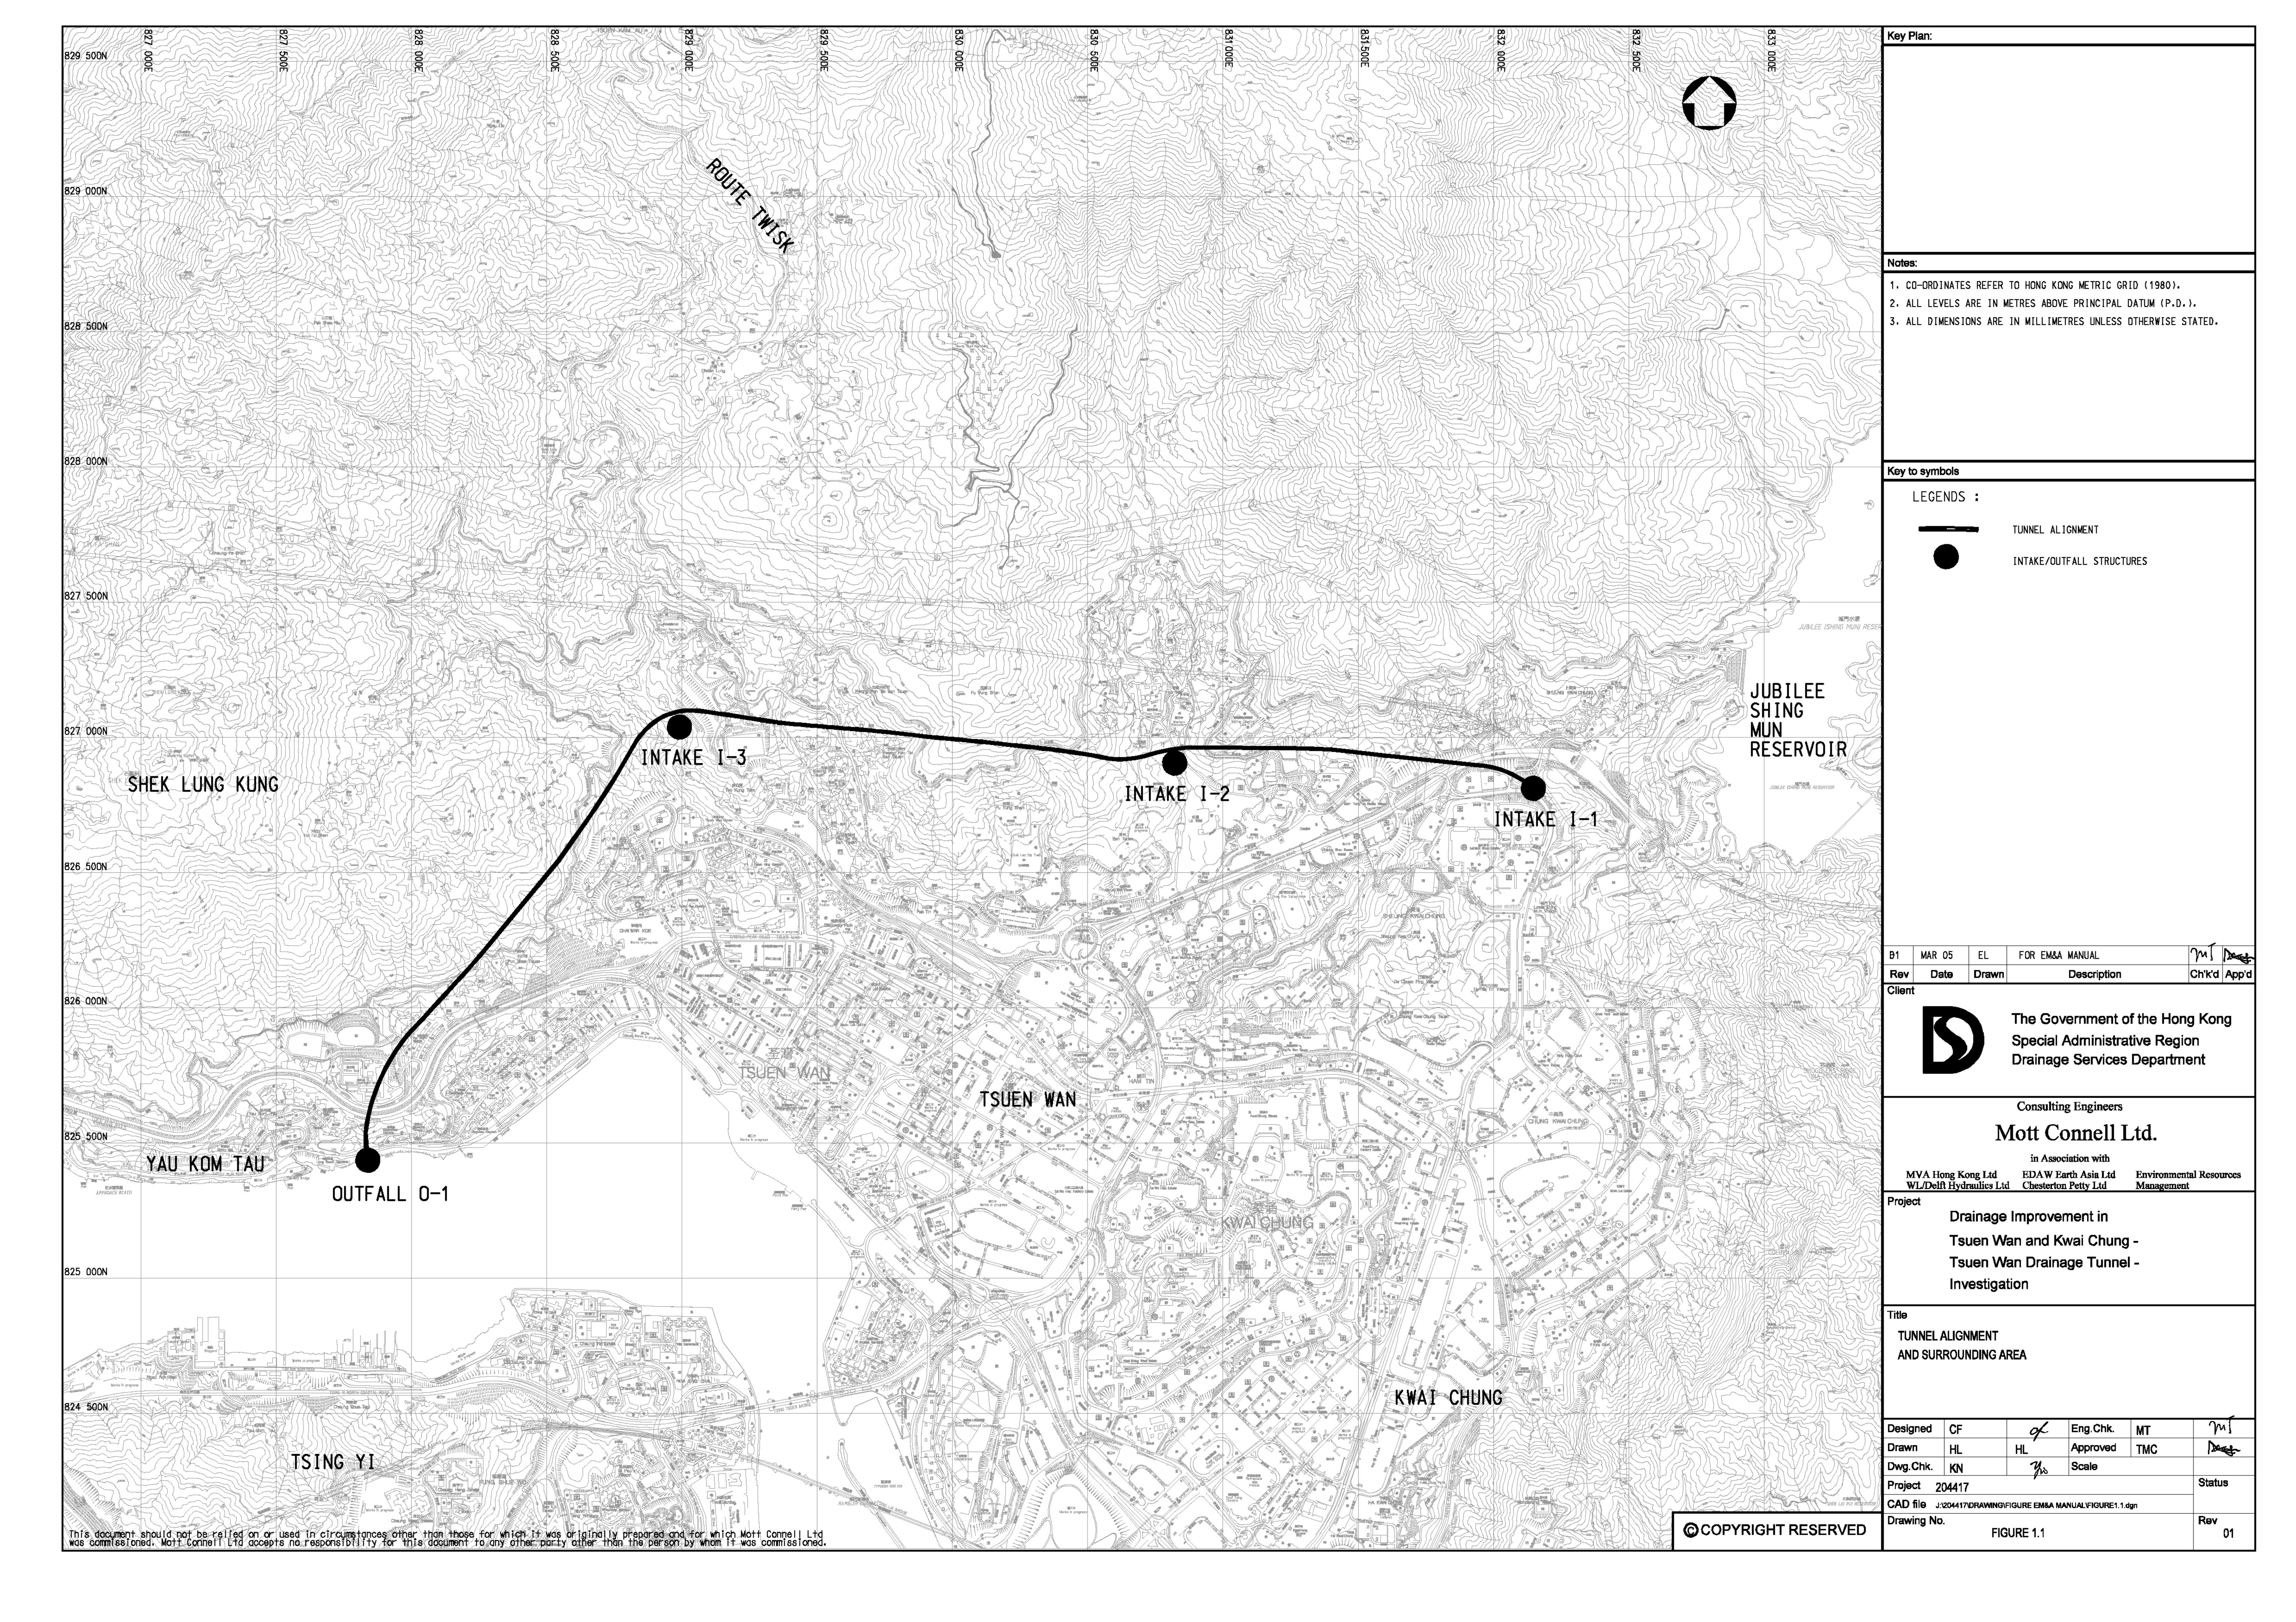



Appendix B

Organization Chart

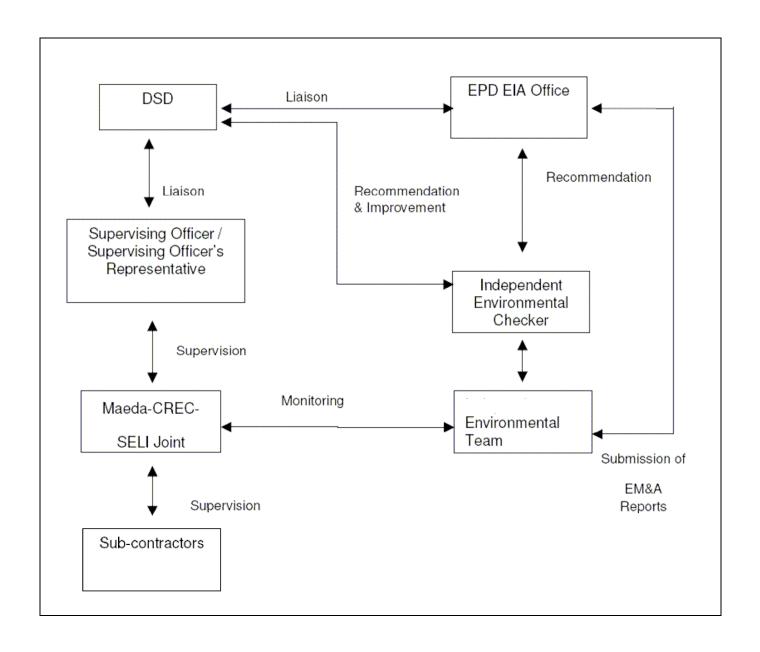

document2 1:1



Appendix C

Work Programme

Preliminaries	Start, Finish (D. Front Da	FM AMBOLA (SOUND STEM AN AN ASSOCIATION DATE MANAGEMENT OF THE MAN
01R0000002 Tender Issue Date 0 01R0000004 Tender Closing Date 0 01R0000006 Letter of Acceptance Issued Date 0 01R0000008 Contract Commencement Date 0	0	• • • • • • • • • • • • • • • • • • • •
Completion of Section 1 of the Works Completion of Section 2 of the Works Completion of Section 3 of the Works	27JUL11* 2 0 714 27JUL11* 2 0 27JUL11* 2 0	days after LOA 1308 days from DOC including DOC◆ 1308 days from DOC including DOC◆ 1308 days from DOC including DOC◆
01R0000016 Completion of Section 4 of the Works 0 01R0000018 Completion of Section 5 of the Works 0 01R0000020 Completion of Section 6 of the Works 0 01R0000022 Completion of Section 7 of the Works 0	0 0 0 0	including including including
<u> </u>	26MAR08 2 0	n.
	26MAR08 2 0 26MAR08 2 0 26MAR08 2 11 26MAR08 2 0 28DEC07 2 0	
01R00E0102 Possession of Portion E - 650d of DOC 0 01R00E0102 Possession of Portion E - 650d of DOC 0 01R00E0104 Handover of Portion E 0 01R00F0102 Possession of Portion F on DOC 0 01R00G0104 Handover of Portion G 0 01R00G0104 Handover of Portion G 0	4 4 61 70	
01R0010102 Possession of Portion I on DOC 0 01R0010104 Handover of Portion I 0 01R00J0102 Possession of Portion J 0 01R00J0104 Handover of Portion J 0 01R00H10102 Possession of Portion H1 on DOC 0	2 2 2 2 2	The exact date to be agreed with WSD WSD Tunnel ShutdownER 4.2.10 (6) allows 50 days from the date of
Start Date 24SEP12 Finish Date 24SEP12 Data Date 14DEC07 Recommended Bar 14DEC	TWD1 Maeda-CREC-SELI JV CONTRACT NO. DC/2007/12 Design and Construction of Tsuen Wan Drainage Tunnel Draft Works Programme	Sheet 1 of 42 Sheet 1 of 42 13FE038 Revision 1 Revision Checked Approved not

	2 0	24SEP12	26AUG12	30	Demolish & removal of Contractor's main office	01R0001408
	- 0	2541612	154 PRO8	4 504	Maintain & Service the Contractor's office	01 10001404
. 3		├	28DEC07	30		01R0001402
		1				
	2 0	24SEP12	26AUG12	30	Demolish & removal of Principle Office	01R0000320
	2 0		1	1,673	- 1	01R0000319
	2 0	25A		1,688	!	01R0000318
	2 0	25AI		1,585	1	01R0000316
	2 0	25AUG12	<u> 1</u>	1,594	. Į	01R0000314
Eswithin 1 month of DOC	2 0			30	Provide survey equipments as per App. ER,M	01R0000311
ER 12.4; 3 nos. vehicles within 14 days of DOC2 nos. vehicles after 3 months of DOC	2 0	26MAR08	28DEC07	06	Provide transport for the SO as per App. ER,M	01R0000310
Extension more than 2 months after the instruction	2 0	16MAY08	14MAR08	94	Provide secondary offices, directed by SO	01 R00000308
Fermily the satisfaction of the SO	1	14APR08	28JAN08	8	Erect SO's principle office in Portion H1/H2	01R0000306
<u>.</u>	1	11MAR08	28JAN08	35	5 Erect Hoarding/Signboard/Gate/Fencing	01R0000305
To the satisfaction of SOsubmit detailed propasal within 3 weeks of LOA	2	26JAN08	28DEC07	8	Design the SO's principle office	01R0000304
to the satisfaction of the SO ER 12.3.1 refers	2 1	03JAN08	28DEC07	7	Provide temporary accommodation	01R0000302
					ensilitation de Stores pellegale	
	, 2 , 0	25AUG12	27JUL12	30	3 S7-Maintenance Period (30 days)	01R7000228
Variable of the second	2 0	: 26JUL12	,673 28DEC07	1,673	S7-Ladscape softworks & establishment works	01R7000226
Command control of the control of th	2 0	25JUL12	27JUL11	365	4 S6-Maintenance Period (365 days)	01R60G0224
Control of the Contro	2 0	26JUL11	26NOV09	909	2 S6-Works within Portion G	01R60G0222
Comparation of the Comparation o	2 0	26JUL12	28JUL11	365	0 S5-Maintenance Period (365 days)	01R50D0220
	2	27JUL11	1,308 28DEC07	1,308	8 S5-Slope Stabilization works within Portion D	01R50D0218
The control of the co		25JUL12		365	6 S4-Maintenance Period (365 days)	01R40C0216
	2 0	26JUL11	26MAR08	1,218	4 S4-Slope Stabilization works within Portion C	01R40C0214
The Control of the Co	ļ	25.		365	2 S3-Maintenance Period (365 days)	01R30B0212
	2 0	26JUL11	26MAR08	1,218	0 S3-Stope Stabilization works within Portion B	01R30B0210
	2	25	27JUL11	365		01R20A0208
	<u> </u> 	26	1,218 26MAR08	1,218	6 S2-Slope Stabilization works within Portion A	01R20A0206
	ļ	26JUL12	28JUL11	365	4 S1-Maintenance Period (365 days)	01R1000204
	2 0	27JUL11	28DEC07	1,308	S1-Works in Portions A to F except works in S2-7	01R1000202
	2 0	24SEP12		0	4 Handover of Portion H2	01R0H20104
	2 0		22OCT08	0		0130H20102
TO THE WAY THE WAY THE WAY THE WAY THE WAY THE WAY TO SHOW THE WAY THE	2	24SEP12		0	Handover of Portion H1	01R0H10104
DIFMANDA ASSONDU EMAM UKISDINDI KMAMUKISTIN KONDU KMAMUKISDI MAMUKISDI KMAMUKI KOD	Cal Total		Start	Orig	Activity	
SAME TO SAME THE SAME SAME SAME SAME SAME SAME SAME SAM	\$					

All Market and All Ma		
DESCRIPTION OF THE PROPERTY OF	Serie District	AMINASOD
Works Programme & Manthy Reportes perso		ocaraciana reco
	7 14DEC07 20DEC07 2 0 8	
ŀ	e 14 21DEC07 03JAN08 2	
i	14 14DEC07 27DEC07	
- 1	7 04JAN08 10JAN08 2 0	
- 1		
- 1	-	
01R0000514 Contractor's Monthly Progress Report	2	www.mercentalto be
Safety Plan as par 500 thin		Commence of the Commence of th
ON DOMANDO ON THE STATE OF THE		
	14 14DEC07 27DEC07 2	
	7 28DEC07 03JAN08 2 7 Within	
	35 14DEC07 17JAN08	
	1,682 18JAN08 25At	
17/H0000602 Fulfill all relevant safety obligation	1,703 28DEC07 25AUG12 2 0 CONTRACTOR OF THE PROPERTY OF THE PR	
101 HOUDO/04 SUbmit documents for all insurances are effected	3d 21 14DEC07 03JAN08 2 0 Pas per SCC9 SCC10 8 SCC45	
	PLEASURE DE MAN CONTROL PLAN A CONTR	
T	14 28DEC07 10JAN08 2 0 as per SCC 74 withfin 14 days of DOC	
	28 14DEC07 10JAN08 2	
	2 0 Bwithir	· · · · · · · · · · · · · · · · · · ·
01R0000808 Maintain & update Quality System	0	dy themselves to describe
EnViloument		
01R0000902 Nominate Environmental Officer	14 14PEC07 97PEC07 0 PEC B 1 CL	
	140EC07 03 IANDS 2 0	
01R0000904 Submit draft EMP	14DEC07 03.IAN08 2 0	
01R0000906 Revise draft EMP within 7 days of SO's notice	04JAN08 17JAN08 2	
01R0000908 Submit final version of EMP	14DEC07 27JAN08 2 0 Mas ne	
01R0000910 Review/update/submit EMP monthly	2 28JAN08 26JUL12 2 0	
	03JAN08 2	Owner control or and a second
01R0000914 Submit Baseline Monitoring Plan	28DEC07 17JAN08 2 0	•
01R0000915 Seek for EPD's Agreement on WQML & schedule	21 18JAN08 07FEB08 2 0 F	
- 1	-	
	20 27FEB08 17MAR08 2 0 Efer approval of the SO	: 1
- 1	1,592 18MAR08 26JUL12 2 0	
17R0000902 Fulfill all relevant environmental obligation	1,673 28DEC07 26JUL12 2 0	

Controlled Personal Library Controlled Controlled	Activity Description	Original Early Fearly Col Total Control 2008 Control Col Col Control Col Col Col Col Col Col Col Col Col C
Machine Mac	Excelvation Permittotilles per Scioss. & Scioss	120 000 000 000 000 000 000 000 000 000
10 Schort I benefit time of LUS reflection experiment 1 2 ELECTY LUANNIN 2 27 28 28 28 28 28 28		14DEC07 20DEC07 2 0 as per SCC83; within 7 days of LOAlternet Interface Utility Management
10 State of the control of the		21DEC07 03JAN08 2 21 M
Committee of the company of the co		28DEC07 03JAN08 2 22
12 Appoint a Auditived Structural Expinent 2 2 14,040 2 2 2 14,040 2 2 2 14,040 2 2 2 2 2 2 2 2 2	i	04JAN08 24JAN08 2 22
12 Population of NAT trough in the SOLOSO 7 STATEON S	- !	04JAN08 24JAN08 2
16 Reser of Yep/Leading Development 20 Office Order 20	l	25JAN08 31JAN08 2 22
Item		01FEB08 20FEB08 2 22 EFR.B11.18A3(1): not less than 17 working
22 Appoint a Austlifed Structural Engineer 30 280EGOT 26AAN08 2 Ames per Eh. B1 1.61	01R0001016 Issue of XP	20FEB08 2 22 🔷
Of Shorth a Aualified Structural Engineer 30 22DECOTY 23LANNB 2 4 Figure 1 5 4 Bit 1 61; within 30 days of DOC 08 Propose schedule response schedule and report of the processing of the schedule of the processing of the schedule of t	Presonstruction Gondition Sulvey	
Compared to the controller survey 22 2005COT 224ANNS 2 1 15 15 15 15 15 15		
Cary of the Percentation Confident Survey 20 2015CO2 2015		28DEC07 26JAN08 2 4
Description contained named and state 2 0.00	ļ	28DEC07 26JAN08 2 4
Papere shaftmiff reports for pre-constitution C.S. 22 OSFEEDB CTMANOB 1 2	-	28JAN08 28APR08 1
Q2. Appoint Traffic Consultant/Traffic Engineer 14 14DECOT 32DECOT 22DECOT 23DECOT 23DE	-	05FEB08 07MAY08 1 3
Quality Traffic Consultant/Traffic Engineer 14 14DECO7 27DECO7 27DECO7 2 Process 4 Process<	Traffle	
Prepare/submit TA Schemes (rightes & egress)		14DEC07 27DEC07
1	1	28DEC07 03JAN08
16. Obtain endorsament of TTA schemes by the Authorities 2 of 09FEBOS 2 × 18.4A/08 2 × 7 Emytors of 17.5 (9) refers 27. Approval of TTA schemes by the Authorities 2 of 09FEBOS 25.4UG12 2 × 0 Emytors of 09FEBOS 25.4UG13 2 × 0]	04.IANDR 17.IANDR
22 Submit a Sub-contractor Management Plan 30 (44DECO7 12/AN06) 1 2 7 (24DECO7 12/AN06) 2 7 (24DECO7 12/AN06) 2 7 (24DECO7 12/AN06) 2 7 (24DECO7 12/AN06) 2 8 (24DECO7 12/AN06) 3 8 (24DECO7 12/AN06) 4 (24DECO7 12/AN06) 2 8 (24DECO7 12/AN06) 4 (24DECO7 12/AN06) 2 8 (24DECO7 12/AN06) 2 8 (24DECO7 12/AN06) 3 8 (24DECO7 12/AN06) 3 8 (24DECO7 12/AN06) 4 (24DECO7 12/AN06) <		18.1ANOR OZEEBOR 2
2 Submit a Sub-contractor Management Plan 30 14DEC07 12JAN08 2 0	7	OBFFEROR OGMABOR 2 7 MEHVY & Police FIR B1 1 15
22 Submit a Sub-contractor Management Plan 30 14DECO7 12JAN08 2 0	Control of the second s	
22 Submit a Sub-contractor Management Plan 30 14DEC07 12JAN08 2 0 0		
24 Submit Quarterly the Updated SMP 1,597 12APR08 22AUG12 2 0 22 Approval of Landscape Specialist Contractor 7 SBDECO7 27/DEC07 2 SBDECO7 27/DEC07 2 SBDECO7 27/ABV08 2 SBDECO7 28 SBDECO7 28 SBDECO7 28 SBDECO7 2 SBDECO7<	1	14DEC07 12JAN08 2 0
22 Appoint Landscape Specialist Contractor 14 IADEC07 27DEC07 2 RBEC07 3 ABACOB 2 RBEC07 3 ABACOB 3 ABACOB 3 ABACOB 3 ABACOB 4	, 1	25AUG12 2 0
22 Appoint Landscape Specialist Contractor 14 14DEC07 27DEC07 27DEC07 2 83 2 4 34 SO's Approval of Landscape Contractor 7 28DEC07 03JAN08 2 83 2 28 2 28 2 36 Nominate competent person to oversee tree works 45 14DEC07 27JAN08 2 59 2ERB 26.02A; within 3 mbhs from DOC 28 28 28 28 28 28 28 28		
22 Appoint Landscape Specialist Contractor 14 14DEC07 27DEC07 2 83 8 34 SO's Approval of Landscape Contractor 7 28DEC07 23JAN08 2 83 8 9 8 8 8	. 1	
34 SO's Approval of Landscape Contractor 7 28DECO7 03JAN08 2 83 1 36 Nominate competent person to oversee tree works 45 14DECO7 27JAN08 2 59 □ ERBR 26.024; within 45 dyas of LOA □ 10 Obtain Tree Removal Permit by Others 90 28DECO7 26MAR08 2 0 □ □ □ □ □ □ □ □ □ □ □ □ □ □ □ □ □ □ □	- 1	14DEC07 27DEC07 2
36 Nominate competent person to oversee tree works 45 14DEC07 27JAN08 2 59 STERR 26.02A; within 45 dyas of LOA 10 Obtain Tree Removal Permit by Others 90 28DEC07 26MAR08 2 0 →ER 1.5.3 (2); within 3 mpts from DOC C 2 Remove / Transplant Trees start 0 27MAR08 2 0 →ER 1.5.3 (2); within 3 mpts from DOC C 2 Appoint Surveyors 14 28DEC07 10JAN08 2 17 R AER 1.5.3 (2); within 3 mpts from DOC R 4 SO'S Approval of Surveyor 14 28DEC07 10JAN08 2 17 R		28DEC07 03JAN08 2
10 Obtain Tree Removal Permit by Others 90 28DEC07 26MAR08 2 0	ļ	14DEC07 27JAN08 2 59 TWEFR 26.02A; within 45 dyas of LOA
12 Remove / Transplant Trees start 0 27MAR08 2 0 ◆ER 1.5.3(2) within 3 months from DOC 22 Appoint Surveyors 14 28DECo7 10JAN08 2 17 8 17JAN08 2 17 8 17JAN08 2 17 8 17JAN08 2 17 1 <		28DEC07 26MAR08 2 0 Emme R 1.5.3 (2); within 3 mbhs from DOC
22 Appoint Surveyors 14 28DEC07 10JAN08 2 17 8 14 SO'S Approval of Surveyor 7 11JAN08 17JAN08 2 17 8 8 Initial Survey 28 18JAN08 22FEB08 1 14 Extraction of Survey works 0 Maintain & carry out survey works 1,000 23FEB08 11JUL11 1 14 Extraction of Survey works	2	27MAR08 2 0 +
Appoint Surveyors 14 28DEC07 10JAN08 2 17 8 SO's Approval of Surveyor 7 11JAN08 2 17 8 Initial Survey 28 18JAN08 22FEB08 1 14 8 Maintain & carry out survey works 1,000 23FEB08 11JUL11 1 14 8	SINVE	
1 20 20 1 20 20 1 20 20	1	CONTRACTOR TO TAKE
Maintain & carry out survey works 1,000 23FEB08 11JUL11 1 14 EMERGED STEEDS 11JUL11 1 15	T-	SOUPCO! CONTROL
Maintain & carry out survey works 1,000 23FEB08 11JUL11 1 14	- T	11JAN08 17JAN08 2 17
Maintain & Carry out Survey works		18JANU8 ZZFEBU8 1 14 E
	- 1	23FEB08 11JUL11 1 14

	2 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	E30 30.06(2) E3
01R0001944 Produce 2 documentary video for tunnel	28JUL11 26AUG11 2	Marked 25 per EH4.4.12
01R0002202 Prepare/submit preliminary CRA 01R0002204 SO's acceptance of preliminary CRA 01R0002208 Prepare/submit detailed CRA 01R0002208 SO's acceptance of detailed CRA 01R0002208 SO's acceptance of detailed CRA	366 14DEC07 13DEC08 2 9 420 08MARIOB 01MAY09 2 9 418 20APR08 11JUN09 2 9 455 28JUN08 25SEP09 2 9 455 455 25SEP09 2 9 455	Sslon ©DDA submission
01R0002302 Prepare/submit a physical model as per ER 4.4.8 01R0002304 Prepare/submit a 3-D animation model	90 14DEC07 12MAR08 2 0 TENTRO TO TENTRO TO TENTRO TO THE SO TENTRO TO TENTRO T	s per ER's Note 4.4.9

Description	Dur Slar	Finish ID Float	DIN EMAMMERASION DE LEMENAMENTA FISION DE DEMANDE DE MANTENES ON DE ENTAMENTA INTESTO PUDE LE ENTAMENTA DE L'ABITATION DE L'AB
01R0002402 Propose the design of web page	30 28DEC07	26JAN08 2 0	Envithin 1 month from DOC
01R0002404 Produce the web page for approval of SO	30 27JAN08	25FEB08 2 0	within 2 months from DOC
	30 26FEB08	26MAR08 2 0	
01R0002408 Submit updated web pages monthly	1,613 27MAR08	25AUG12 2 0	
รางเรื่องและเป็นสะเจกเลยเก็กสะเก็บการสามารถให้			
01R0002501 1R 1; On provision of SO's Accommodation	0	14APR08 2 1.624	Saccommodation for accupation as ner App. FR M
01-70002502 1R 2; On providing documents of effected CWI	0		Care of the works insurance has been effected
Ī 7	0	03JAN08 2 1,726	Std party insurance has been effected
	0	03JAN08 2 1,726	◆P.1. Insurance has been effected.
Ţ	0	26MAR08: 2 1,643	Aland transpoert delivered for use of the SO
	0	14APR08 2 1,624	Computer facilities for use of the SO
- 1	0	25SEP09 2 1,095	◆detailed CRA incl. pre-condition survey
- 1	0	12MAR08 2 11,657	◆physical model completed as per ER 4.4.8
01R0002509 ;1R 9; On acceptance of 3-D Animation Model	0	12MAR08 2 1,657	◆3-D animation model completed as per ER 4.4.9
01R0002510 1R 10; On satisf. operation of CCTV for 3 mth	0	31JUL08 2 1,516	Of 3 mths of the remote CCTV intalled in Portions A B, C & D as per ER 4.4 10.
01R0002511 1R 11; On acceptance of O&MM	0	300CT11 2 330	O&MM completed as per ER 4.4.11◆
	0	250CT11 2 335	built drwgs. completed as per ER 4.4.12
	0	26AUG11 2 395	tunnel report & vedeo & brother submitted as per ER 4.4.13
	0	27MAR08 2 1,582	of all obligations by this C.S. 3-mths from DOC
Ī	0	2	♦of all obligations by this CS 6 miths from DOC
Ť	0	25SEP08 2 1,400	♦of all obligations by this CS 9 mths from DOC
	0		of all obligation by this CS 12 mths frm DQC
	0	27MAR09 2 1,217	of all obligations by this CS 15 mths frm DOC
	. 0		of all obligations by this CS 18 mths frm DOC
Ī	0	2	Or all obligations by this CS 21 mths frm DOC
\neg	0	8	of all obligations by this CS 24 mths frm DOC
Ì	0	2	of all obligations by this CS 27 mths fm DOC
	0	2	On this CS 30 miles from DOC
1	0	2	of all obligations by this GS 33 mths frm DOC
- " 	0	26DEC10 2 578	of all obligations by this CS 36 mths frm DOC◆
	0	27MAR11 2 487	of all obligations by this CS 39 mths frm DOC.
	0	26JUN11 2 396	of all obligations by this CS 42 mths frm DOC.
1	0	25SEP11 2 305	of all obligations by this CS 45 mths frm DOC◆
	0	13AUG11 2 408	of completion axcept:Section 7.◆
	0	260CT11 2 334	of all obligations 3 mths frm DOM excl. Sec. 7.
	0	25JAN12 2 243	of all obligations 6 mths frm DOM excl. Sec. 7
	0	25APR12 2 152	of all obligations 9 miths frm DOM excl. Sec. 7.
Of ROMOSE33 112 33: On issuance of maintenance confidents	c	05.010.40	♣ otcollition

Acivin Len	EAN EANY CAL TOTAL
33.5	Sark. Finsh 10 Foat 7 8 9 10111 2131 41 61 617 161 9202 1222 2627 262 2031 3203 435 59 97 38 94 07 42
02L10D0114 Approval of Design Checker by the SO	28 11JAN08 07FEB08 2 1
Pest din Pero (eight to Mail (silin) Pendian (p	
	14 17JAN08 30JAN08 2 2 8
02L1DD0104 Design certification by the Design Checker	14 01FEB08 14FEB08 2 1 8
02L1DD0106 Design submission for the SO's approval	1 15FEB08 15FEB08 1
02L1DD0108 Design review by the SO	28 16FEB08 14MAR08 2 2 E
02L1DD0110 Obtain design approval from the SO	0 14MAR08 2 2 +
Boulder Assessment & Design for Stabili. Measure	
02L1DD0302 Design preparation for the AIP submission	15 31JAN08 14FEB08 2 3 B
02L1DD0304 Design (AIP) certification by the Design Checker	14 15FEB08 28FEB08 2 19 %
02L:1DD0306 Design (AIP) submission for the SO's approval	1 29FEB08 1 16
02L1DD0308 Design (AIP) review by the SO	14 01MAR08 14MAR08 2 19 E
02L1DD0310 Obtain design (AIP) approval from the SO	0 14WAR08 2 19
02:L1DD0312 AIP submission for rel. authorities' approval	1 15MAR08 1 13 1
02L1DD0314 Design (AIP) review by the rel. authorities	28 16MAR08 12APR08 2 20 🖾
02L1DD0316 Obtain rel. authorities's approval for AIP	1 14APR08 14APR08 1 16
02L1DD0318 Obtain SO's consent for design (AIP)	
02L1DD0320 Design preparation for the DDA submission	30 24MAR08 22APR08 2 20 INT.
02L1DD0322 Design (DDA) certification by the Design Checker	2
02L1DD0324 Design (DDA) submission for the SO's approval	
02L1DD0326 Design (DDA) review by the SO	14 08MAY08 21MAY08 2 20
1	. 21MAY08 2
	1 22MAY08 22MAY08 1 16
	28 23MAY08 19JUN08 2 20
i	1 20JUN08 20JUN08 1 16
02L1DD0336 Obtain SO's consent for design (DDA)	0 21JUN08 2 20
Site Formation Design; +69mPD to +40mPD	
02L1DD0402 Design preparation for the AIP submission	14 17JAN08 30JAN08 2 2 F
02L1DD0404 Design (AIP) certification by the Design Checker	14 27JAN08 09FEB08 2 2 PM
02L1DD0406 Design (AIP) submission for the SO's approval	1 11FEB08 1 1
02L1DD0408 Design (AIP) review by the SO	14 12FEB08 25FEB08 2 1
02L1DD0410 Obtain design (AIP) approval from the SO	0 25FEB08 2 1
02L1DD0412 AIP submission for rel. authorities' approval	1 26FEB08 26FEB08 1 1 1
02L1DD0414 Design (AIP) review by the rel. authorities	12 27FEB08 09MAR08 2 1 H
	1 10MAR08 10MAR08 1 1
02L1DD0418 Obtain SO's consent for design (AIP)	0 11/MAR08 2 1 ◆
1	
	14 12MAR08 25MAR08 2 1
02L1DD0424 Design (DDA) submission for the SO's approval	1 26MAR08 26MAR08 1 1
į	14 27MAR08 09APR08 2 1
102L1DD0428 Obtain design (DDA) approval from the SO	0 09APR08 2 1

AINEX	Pig .	Orig Early Early Ca		OTENIEN EINES MED DER REGENERAL BESTANDEREN KANNEL EN KONDER MEN KANNEL AKSIONED HENNAMPROAKS SOO
1021 1000430 DDA cubmission for rel authorities' approved	A CONTRACTOR OF THE PARTY OF TH		7 7 7 Y	8 9 10 11 2 3 14 15 8 17 8 19 20 2 12 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2
- 1	- 5		- ,	
	7 ,			
שבריו טייטיין אין אין אין אין אין אין אין אין אין	-	Z3AFHUB Z3AFHUB 1		
02L1DD0436 Obtain SO's consent for design (DDA)	0	24APR08 2	-	The control of the co
•				
	14		ന	
- 1	14	29FEB08 13MAR08 2	m	36
02L1DD0506 Design (AIP) submission for the SO's approval	-	14MAR08 14MAR08 1	2	
	14	15MAR08 28MAR08 2	က	
	0	28MAR08 2	က	
02L1DD0512 AIP submission for rel. authorities' approval	-	29MAR08 29MAR08 1	Ø	
02L1DD0514 Design (AIP) review by the rel. authorities	24	30MAR08 19APR08 2	60	
	-	21APR08 21APR08 1	23	
- 1	0	22APR08 2	2	•
02L1DD0520 Design preparation for the DDA submission	14	16APR08 29APR08 2	CVI	136
02L1DD0522 Design (DDA) certification by the Design Checker	14	30APR08 13MAY08 2	7	
02L1DD0524 Design (DDA) submission for the SO's approval	-	14MAY08 14MAY08 1	2	
02L1DD0526 Design (DDA) review by the SO	14	15MAY08 28MAY08 2	2	
02L1DD0528 Obtain design (DDA) approval from the SO	0	28MAY08 2	7	•
02L1DD0530 DDA submission for rel. authorities' approval		29MAY08 29MAY08 1	CJ	
02L1DD0532 Design (DDA) review by the rel. authorities	21	30MAY08 19JUN08 2	က	
02L1DD0534 Obtain rel. authorities's approval for DDA	-	20JUN08 20JUN08 1	2	
02L1DD0536 Obtain SO's consent for design (DDA)	0	21JUN08 2	60	· · · · · · · · · · · · · · · · · · ·
Site Formation Design; +24mPD to 14mPD				
02L1DD0602 Design preparation for the AIP submission	14	29FEB08 13MAR08 2	32	
	14	14MAR08 27MAR08 2	25	255
	-	28MAR08 28MAR08 1	ଯ	
ī	44	29MAR08 11APR08 2	83	
	0		ĸ	
\neg	-	12APR08 12APR08 1	ສ	
	88	13APR08 10MAY08 2	52	िंड
02L1DD0616 Obtain rel. authorities's approval for AIP		13MAY08 : 13MAY08 1	23	
	0	14MAY08 2	ន	•
02L1DD0620 Design preparation for the DDA submission	44	08MAY08 21MAY08 2	ន	
02L1DD0622 Design (DDA) certification by the Design Checker	14	22MAY08: 04JUN08 2	ສ	ESS
02L1DD0624 Design (DDA) submission for the SO's approval	-	05JUN08 05JUN08 1	⊕	
02L1DD0626 Design (DDA) review by the SO	4	06JUN08 19JUN08 2	24	
02L1DD0628 Obtain design (DDA) approval from the SO	0	19JUN08 2	24	•
02L1DD0630 DDA submission for ref. authorities' approval	-	20JUN08 20JUN08 1	19	
	58	21JUN08 18JUL08 2	24	
	7-	19JUL08 19JUL08 1	20	
02L1DD0636 Obtain SO's consent for design (DDA)	0	21JUL08 2	23	•

ID ACTIVITY Description	Orig Early Cal (Original Property Col (Original Property Col Start) Finish (Original Property Col	MONTHAN CIND SEMAMININANS
TBM Launching Chamber Design	Managara Ma	74819505152535455585758598061626364656
02L1DD0702 Design preparation for the AIP submission	15 14MAR08 28MAR08 2 36 R	F 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1
- 1	15 29MAR08 12APR08 2 36 B	
,	1 14APR08 14APR08 1 281	
- 1	30 15APR08 14MAY08 2 35	
	14MAY08 2	
	1 15MAY08 15MAY08 1 29	
02L1DD0716 Obtain ref. authorities's approval for AIP	1 13JUN08 13JUN08 1 29	
T	0 14JUN08 2 35	11.000
r	ļ ļ	
-7	30 08JUL08 06AUG08 2 35 83	
	1 07AUG08 07AUG08 1 30	
	28 08AUG08 04SEP08 2 35 B	
	1 05SEP08 05SEP08 1 27	
02L1DD0736 Obtain SO's consent for design (DDA)	0 06SEP08 2 36	
Hopper Foundation Design		
02L1DD0802 Design preparation by the Designer	ļ	
3 1	15 12JUN08 26JUN08 2 77	
02L1DD0806 Design submission for the SO's approval	١.,	
02L1DD0808 Design review by the SO	30 28JUN08 27JUL08 2 77	
02L1DD0810 Obtain design approval from the SO	27JUL.08	
Steel Platform & Hopper Design		
- 1	30 12JUN08 11JUL08 2 47	
	15 12JUL08 26JUL08 2 47 R	
	28JUL08	
	30 29JUL08 27AUG08 2 46	
02L1DD0910 Obtain design approval from the SO	0 27AUG08 2 46	
Overhead Gantry Support & Noise Enclosure Design		
02L1DD1002 Design preparation by the Designer	30 28APR08 27MAY08 2 47 國	
02L1DD1004 Design certification by the Design Checker	15 28MAY08 11JUN08 2 60	
02L1DD1006 Design submission for the SO's approval	1 12JUN08 1 50	
02L1DD1008 Design review by the SO	30 13JUN08 12JUL08 2 60	-
	0 12JUL08 2 60 �	
	14JUL08 1	
	28 15JUL08 11AUG08 2 59	
	1 12AUG08 1 48	
02L1DD1018 Obtain SO's consent for design	0 13AUG08 2 60 +	

ID Activity The criticism	Original Early Cal Total Distriction	MANNELIJASIGINDIVEIMANNINIASIGINIDJIEMANNINIASIGINIDI EMAMATATA SIGNID KENAMALA ASIGO
ELS Design for Spiral Ramp & Vehicular Access		U. 11.41.91.11.19.11.19.12.44.18.4.22.47.17.4.34.4.18.4.34.4.19.4.4.4.4.4.4.4.4.4.4.4.4.4.4.4.4.4
02L1DD1102 Design preparation for the AIP submission	30 29MAR08 27APR08 2 47	
02L1DD1104 Design (AIP) certification by the Design Checker	21 28APH08 18MAY08 2 130	E
02L1DD1106 Design (AIP) submission for the SO's approval	1 19MAY08 19MAY08 1 109	
	5	
- 1	0 18JUL08 2 130	•
02L1DD1112 AIP submission for rel, authorities' approval	1 19JUL08 19JUL08 1 108	
02L1DD1114 Design (AIP) review by the rel. authorities	21 20JUL08 09AUG08 2 130	
02L1DD1116 Obtain rel. authorities's approval for AIP	1 11AUG08 11AUG08 1 108	
02L1DD1118 Obtain SO's consent for design (AIP)	0 12AUG08 2 129	•
02L1DD1120 Design preparation for the DDA submission	30 21JUL08 19AUG08 2 129	
02L1DD1122 Design (DDA) certification by the Design Checker	28 20AUG08 16SEP08 2 129	
02L1DD1124 Design (DDA) submission for the SO's approval	1 17SEP08 17SEP08 1 106	
02L1DD1126 Design (DDA) review by the SO	60 18SEP08 16NOV08 2 130	
02L1DD1128 Obtain design (DDA) approval from the SO	0 16NOV08 2 130	
02L1DD1130 DDA submission for rel. authorities' approval	17NOV08 17NOV08 1 106	
02L1DD1132 Design (DDA) review by the rel. authorities	28 18NOV08 15DEC08 2 130	
02L1DD1134 Obtain rel. authorities's approval for DDA	16DEC08 1	
02L1DD1136 Obtain SO's consent for design (DDA)	17DEC08 2	
ELS Design for Box Culvert & Open Channel		The state of the s
021.10D1202 Design preparation for the AIP submission	30 12JUL08 10AUG08 2 262	
	09SEP08 2	
02L1DD1206 Design (AIP) submission for the SO's approval	1 10SEP08 10SEP08 1 209	
02L1DD1208 Design (AIP) review by the SO	60 11SEP08 09NOV08 2 263	
02L1DD1210 Obtain design (AIP) approval from the SO	0 09NOV08 2 263	
02L1DD1212 AIP submission for rel. authorities' approval	1 10NOV08 10NOV08 1 212	
02L1DD1214 Design (AIP) review by the rel. authorities	28 11NOV08 08DEC08 2 263	
02L1DD1216 Obtain rel. authorities's approval for AIP	1 09DEC08 09DEC08 1 212	
02L1DD1218 Obtain SO's consent for design (AIP)	0 10DEC08 2 264	
02L1DD1220 Design preparation for the DDA submission	30 18NOV08 17DEC08 2 264	
02L1DD1222 Design (DDA) certification by the Design Checker	30 18DEC08 16JAN09 2 264	
02L1DD1224 Design (DDA) submission for the SO's approval	1 17JAN09 17JAN09 1 213	
02L1DD1226 Design (DDA) review by the SO	. 60 18JAN09 18MAR09 2 264	
02L1DD1228 Obtain design (DDA) approval from the SO	21	
02L1DD1230 DDA submission for ref. authorities' approval	1 19MAR09 19MAR09 1 215	
02L1DD1232 Design (DDA) review by the rel. authorities	28 20MAR09 16APR09 2 264	
02L1DD1234 Obtain rel. authorities's approval for DDA	1 17APR09 17APR09 1 216	
02L1DD1236 Obtain SO's consent for design (DDA)	0 18APR09 2 264	
Design Packages for Workship Partion F		
Main Tunnel Design		
	08FEB08 08MA	
02L1FF0104 Design (AIP) certification by the Design Checker		
	0.000	

25MARO8 1 24MAYO8 2 24MAYO8 2 26MAYO8 1 25JUN08 1 25JUN08 2 17JUL08 2 17JUL08 2 16SEP08 2 16SEP08 2 17JUL08 2 17OCT08 2 10JUN08 1 10JUN08 1 10JUN08 2 22APR08 2 10JUN08 2 10JUN08 1 10JUN08 2 10JUN08 2 10JUN08 2 10JUN08 2 10JUN08 2 10JUN08 1 10JUN08 1 10JUN08 2 11JUN08 3 11JUN08 3 11JUN08 3 11JUN08 3 11JUN08 3	Activity Description	Orig Early Due Start	Early Cal	Total Ploat	ALEM MANATURA SON DO FEMANDE BASON DE LEMANATORISON DE EMANATURA SON DE AFRAGOS DE PARATORISTOS DE PROPERTORISTOS DE PRO
Design (API) review by the SO Design (API) review by the ret. authorities approval for API 24AUMN0	Design (AIP) submission for the SO's approval	1 25	25M,	-	
Obtain design (AIP) approval from the SO Obtain design (AIP) approval from the SO Obtain design (AIP) approval from the SO Obtain rel. authorities's approval for AIP 1 26MAY08 22JUN08 2 Obtain rel. authorities's approval for AIP 2 2MAY08 22JUN08 2 Obtain rel. authorities's approval for AIP 2 2MAY08 22JUN08 2 Obtain rel. authorities's approval for AIP 2 2MAY08 22JUN08 2 Obtain rel. authorities's approval for AIP 2 2MAY08 22JUN08 2 Obtain Collaboration for the DDA submission for the SOA suproval for AIP 1 18JUN08 1 Obtain Collaboration for the AIP submission for the AIP submission for the SOA suproval for AIP 1 1 1 1 1 1 1 1 1			24MAY08	-	
All Pestumission for real, authorities approval of All Pestumission for real, authorities approval for All Pestumission for real authorities approval for All Pestumission for the DDA submission for the DDA submission for the Lauthorities approval for Dosign (DDA) review by the real authorities approval for Dosign (DDA) review by the real authorities approval for DDA and All Pestumission for real authorities approval for DDA and All Pestumission for the Lauthorities approval for DDA and All Pestumission for the Lauthorities approval for DDA and All Pestumission for the Lauthorities approval for DDA and All Pestumission for the Lauthorities approval for DDA and All Pestumission for the Lauthorities approval for DDA and All Pestumission for the Lauthorities approval for DDA and All Pestumission for the Lauthorities approval for DDA and All Pestumission for the Lauthorities approval for DDA and All Pestumission for the AIP submission for the SOS approval for DDA and All Pestumission for the AIP submission for the SOS approval for Dosign (AIP) review by the real authorities approval for AIP and AIP approval for the SOS approval for Dosign (AIP) review by the real authorities approval for AIP and AIP attribution by the Dosign (AIP) review by the real authorities approval for AIP and AIP attribution by the Dosign (AIP) review by the real authorities approval for AIP and AIP attribution for the SOS approval for AIP and AIP attribution by the Dosign (AIP) review by the real authorities approval for AIP approval for AIP and AIP attribution for the AIP authorities approval for AIP and AIP attribution for the AIP authorities approval for AIP and AIP attributies approval for AIP attributies approval for AIP attributies approval for AIP attributies approval for AIP attributies approval for AIP approval fo		0	: L	-	•
Design (AIP) review by the rel. authorities 227/A4Y08 23JUN08 2 0 4 Obtain SO's consent for design (AIP) 1 24JUN08 23JUN08 1 0 25JUN08 2 0 Design preparation for the DDA submission 1 1 24JUN08 23JUN08 2 0 0 Design (DDA) submission for the DDA submission for the SO's approval 1 1 175EP08 173EP08 1 0 0 Design (DDA) submission for the SO's approval 1 1 175EP08 173EP08 1 0 0 Design (DDA) review by the rel authorities 2 0 175EP08 175EP08 1 0 0 Design (DDA) review by the rel authorities 2 0 175EP08 175EP08 1 0 0 Design (DDA) review by the rel authorities 2 0 175EP08 175EP08 1 0 0 Design (MDA) reparation for the AIP submission of the AIP submission for the SO's approval 1 175EP08 175EP08 1 0 0 Design (AIP) review by the SO 1 1 175EP08 1 0 0 0 0 0 0 0 Design (AIP) review by the SO 2 0 0 0 0 0 0 0 0 0		1 26	:	o	
Obtain SO's consent for design (AP) continues a paproval for AP		- †	23.1	0	
Design (DDA) certification by the Design Checker 15 03JUL06 22JUL08 2 0 Design (DDA) certification by the Design Checker 15 03JUL06 17JUL08 2 0 Design (DDA) certification by the Design Checker 15 03JUL06 17JUL08 2 0 Design (DDA) submission for the DDA submission for the SO's approval in the SO's approval	- 1		24JUN08	0 0	
Design (DDA) certification by the Design Checker 15 03JUL09 17JUL09 2 0 Design (DDA) certification by the Design Checker 1 18JUL09 14JUL09 15 DDA authorities approval from the SO 0 19JUL09 15SEP09 2 0 DDA authorities approval from the SO 0 15JUL09 15SEP09 2 0 DDA authorities approval from the SO 0 15JUL09 15SEP09 2 0 DDA authorities approval from the SO 0 15JUL09 17SEP09 1 0 DDA authorities approval from the SO 0 17SEP09 17SEP09 1 0 Design (DDA) approval from the SO 0 17SEP09 1 0 0 Design (DDA) approval from the SO 0 0 0 0 0 0 Design (AIP) evilew by the RAT Tau WITWN 1 23APR09 22APR09 2 107 Design (AIP) evilew by the SO 0 0 0 0 0 0 0 0 0 Design (AIP) evilew by the SO 0 0 0 0 0 0 0 0 0	T		02,101.08	> C	
Design (DDA) submission for the SO's approval 1 i3,UL08 1 i3,UL08 1 is offered 1 is offered <th></th> <th>· }</th> <th>17JUL08</th> <th>0</th> <th></th>		· }	17JUL08	0	
Design (DDA) review by the SO		1 18	18JU	0	
Obtain design (DDA) approval from the SO			16SE	0	
DDA submission for ret. authorities' approval to DDA submission for ret. authorities a peroval of DDA submission for ret. authorities 2 approval from the SO's approval from the SO'			16SEP08 2	0	•
Design (DDA) review by the rel. authorities 28 18SEP08 50CT08 1 0 0		1 17	SEP08 17SEP08 1	O	
Obtain Cobtain rel. authorities's approval for DDA 1 160CT08 150CT08 1 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0		-	55	0	
Obtain SO's consent for design (DDA)	. !		<u>8</u>	0	
Design (AIP) centification by the Design Checker 15 09MAR09 07APR08 2 107 Design (AIP) centification by the Design Checker 15 08APR08 22APR08 2 107 Design (AIP) centification by the Design Checker 45 24APR08 22APR08 2 107 Design (AIP) submission for the SO's approval 45 24APR08 23APR08 1 107 AIP submission for rel. authorities approval from the SO 0 0 0 07JUN08 2 107 AIP submission for rel. authorities approval for AIP 1 10JUL08 03JUL08 2 105 Obtain Cesign (AIP) review by the rel. authorities 1 10JUL08 03JUL08 2 105 Obtain COs consent for design (AIP) 0 0 1 13UL08 2 105 Design (DDA) review by the rel. authorities approval from the SO submission for rel. authorities approval from the SO 45 03AUG08 1 105 Design (DDA) review by the rel. authorities approval from the SO 0 1 1 17SEP08 1 1		0		0	
Design preparation for the AIP submission 30 09MAR08 07APR08 2 107 EST Design (AIP) certification by the Design Checker 15 08APR08 22APR08 2 107 EST Design (AIP) submission for the SOs approval 45 24APR08 07JUN08 2 107 EST Obtain design (AIP) review by the rel. authorities' approval for AIP 0 10JUN08 10JUN08 1 10 Obtain nesign (AIP) review by the rel. authorities' approval for AIP 1 0 10JUN08 1 10 Obtain Cobrain cell authorities' approval for AIP 0 1 0 10JUL08 2 105 Obtain SO's consent for design (AIP) 0 1 10JUL08 2 105 Obtain Cobrain Cobrai	Impact Assessment on WSD Yau Kam Tau WTW				
Design (AIP) certification by the Design Checker 15 08APR08 22APR08 2 107 Design (AIP) submission for the SO's approval 1 23APR08 22APR08 1 107 Obtain design (AIP) review by the SO 0 0 0 07JUN08 2 107 AND submission for rel. authorities? approval for AIP 1 10JUN08 10JUN08 1 10DN Design (AIP) review by the rel. authorities 28 11JUN08 2 105 Design (AIP) review by the rel. authorities 28 14JUN08 17JUL08 2 105 Design preparation for the DDA submission 30 18JUN08 17JUL08 2 105 Design (DDA) certification by the Design Checker 15 18JUL08 14JUL08 2 105 Design (DDA) certification by the Design Checker 15 18JUL08 15SEP08 1 105 Design (DDA) certification by the Design Checker 15 17SEP08 15 105 Design (DDA) review by the rel. authorities 29 18SEP08 15 105				107	
Design (AIP) submission for the SO's approval 1 23APR08 23APR08 1 88 Design (AIP) review by the SO Obtain design (AIP) approval from the SO 0 0 24APR08 07JUN08 2 107 ◆ AIP submission for rel. authorities' approval from the SO 0 0 10JUN08 1 10JUN08 1 10DUN08 1 10DUN08 1 10DUN08 1		†	22AP	107	
Obsign (AIP) review by the SO 45 24APR08 07JUN08 2 107 APPROB AIP submission for rel. authorities approval from the SO 0 77JUN08 2 107 APPROB 2 107 APPROB 2 107 APPROB 2 107 APPROB 4 APPROB 2 107 APPROB 4 APPROB 4 100 APPROB 4 100 APPROB 4			23AF	88	
Obtain design (AIP) approval from the SO O O7JUN08 2 107 AIP submission for rel. authorities' approval for AIP 1 1 1 1 1 1 1 1 1			02JUN08	107	
AIP submission for rel. authorities' approval 1 10JUN08 1 88 Design (AIP) review by the rel. authorities 28 11JUN08 08JUL08 2 105 Obtain rel. authorities's approval for AIP 1 09JUL08 08JUL08 2 105 Obtain SO's consent for design (AIP) 0 1 10JUL08 2 105 Design preparation for the DDA submission of the Design Checker 15 18JUL08 1 2 105 Design (DDA) submission for the SO's approval 1 02AUG08 02AUG08 1 8 1 Design (DDA) seview by the SO 0 1 17SEP08 1 8 1 105 DbA submission for rel. authorities' approval for DDA 1 17SEP08 1 8 1 105 1 105	1	0		107	•
Design (AIP) review by the rel. authorities 28 11JUN08 08JUL08 2 105 Obtain rel. authorities's approval for AIP 1 09JUL08 0 2 105 1 Obtain SO's consent for design (AIP) 0 10JUL08 2 105 1 Design preparation for the DDA submission 30 18JUN08 17JUL08 2 105 Design (DDA) certification by the Design Checker 15 18JUL08 0 14UC08 2 105 Design (DDA) submission for the SO's approval 45 03AUG08 1 6SEP08 2 105 Obtain design (DDA) review by the rel. authorities' approval 1 17SEP08 1 56 106 Design (DDA) review by the rel. authorities' approval for DDA 1 1 6OCT08 2 106 106 Design (DDA) review by the rel. authorities' approval for DDA 1 1 6OCT08 2 106 106 Obtain rel. authorities' approval for DDA 1 1 6OCT08 2 106 106 Obtain rel. authorities' approval from the SO approval 1 1 6OCT08 2 106 106 Design (AIP) review by the SO 1 2 68MARIO			10JUN08	88	
Obtain rel. authorities's approval for AIP 1 09JUL08 09JUL08 1 87 Obtain SO's consent for design (AIP) 0 16JUL08 2 105 Design preparation for the DDA submission 30 18JUN08 17JUL08 2 105 Design (DDA) certification by the Design Checker 15 18JUL08 07AUG08 2 105 Design (DDA) review by the SO 0 45 03AUG08 12SEP08 2 105 Obtain design (DDA) review by the SO 0 0 17SEP08 1 86 DDA submission for rel. authorities' approval for DDA 1 17SEP08 1 86 Design (DDA) review by the rel. authorities' approval for DDA 1 16OCT08 1 105 Obtain SO's consent for design (DDA) 0 17OCT08 2 106 Obtain SO's consent for design (DDA) 0 17OCT08 2 1 Design (AIP) certification by the Design Checker 15 09MAR108 2 3 Design (AIP) submission for the SO's approval 1 25MAR10			08JUL08	105	
Obtain SO's consent for design (AIP) 0 10JUL08 2 105 Design preparation for the DDA submission 30 18JUN08 17JUL08 2 105 Design (DDA) certification by the Design Checker 15 18JUL08 0.1AUG08 2 105 Design (DDA) submission for the SO's approval 45 0.3AUG08 0.2AUG08 2 105 Design (DDA) review by the SO 45 0.3AUG08 1.5EP08 1 87 DDA submission for rel. authorities approval for DDA 1 1.7SEP08 1.5EP08 1 85 Design (DDA) review by the rel. authorities's approval for DDA 1 1.6OCT08 2 105 Obtain SO's consent for design (DDA) 0 1.7OCT08 2 107 essment on WSD Tal Lam Chung WT No. 3 1 1.6OCT08 2 107 Design (AIP) certification by the Design Checker 15 0.9MAR08 2 3 Design (AIP) review by the SO 50 26MAR08 1 2 Design (AIP) submission for the SO's approval 1 1.4MAY08 <th></th> <th></th> <th>99JL</th> <th>87</th> <th></th>			99JL	87	
Design preparation for the DDA submission 30 18JUN08 17JUL08 2 105 Design (DDA) certification by the Dosign Checker 15 18JUL08 01AUG08 2 105 Design (DDA) submission for the SO's approval 45 03AUG08 16SEP08 2 105 Design (DDA) review by the SO 0 45 03AUG08 16SEP08 2 105 Obtain design (DDA) review by the rel. authorities' approval from the SO 0 17SEP08 1 86 Dosign (DDA) review by the rel. authorities' approval for DDA 1 17SEP08 15 CCT08 1 16 Design (DDA) review by the rel. authorities' approval for DDA 1 1 17OCT08 2 105 Obtain SO's consent for design (DDA) 0 1 17OCT08 2 107 Design preparation for the AIP submission 30 08FEB08 23MAR08 2 3 Design (AIP) certification by the Design Checker 1 25MAR08 25MAR08 2 2 Design (AIP) review by the SO 0 25MAR08 14MAY08			10JUL08	105	•
Design (DDA) certification by the Design Checker 15 18JUL08 01AUG08 2 105 Design (DDA) submission for the SO's approval 1 02AUG08 1 87 Design (DDA) review by the SO 0 45 03AUG08 16SEP08 2 105 Obtain design (DDA) review by the SO 0 17SEP08 1 86 105 DDA submission for rel. authorities' approval for DDA 1 17SEP08 1 86 105 Design (DDA) review by the rel. authorities' approval for DDA 1 1 17OCT08 2 106 Obtain SO's consent for design (DDA) 0 1 <th></th> <th></th> <th>17JUL08</th> <th>105</th> <th></th>			17JUL08	105	
Design (DDA) submission for the SO's approval 1 02AUG08 02AUG08 1 87 Design (DDA) review by the SO 45 03AUG08 16SEP08 2 105 Obtain design (DDA) approval from the SO 0 17SEP08 1 86 DDA submission for rel. authorities' approval for DDA 1 17SEP08 1 86 Obtain rel. authorities' approval for DDA 1 1 15CCT08 2 105 Obtain rel. authorities' approval for DDA 0 1 1 1 1 1 Obtain rel. authorities' approval for DDA 0 1 <t< th=""><th></th><th></th><th>01AUG08</th><th>105</th><th></th></t<>			01AUG08	105	
Design (DDA) review by the SO 45 03AUG08 16SEP08 2 105 Obtain design (DDA) approval from the SO 0 16SEP08 2 105 DAS submission for rel. authorities' approval from the SO besign (DDA) review by the rel. authorities' approval for DDA 1 17SEP08 1 86 Obtain rel. authorities' approval for DDA 1 1 16OCT08 2 105 Obtain SO's consent for design (DDA) 0 1 17OCT08 2 107 essment on WSD Tai Lam Chung WT No. 3 0 1 17OCT08 2 107 design paparation for the AIP submission 30 08FEB08 08MAR08 2 3 Design (AIP) review by the SO's approval 1 25MAR08 25 2 2 Design (AIP) review by the SO 50 26MAR08 2 2 8 Obtain design (AIP) approval from the SO 0 14MAY08 2 2 4 AIP submission for rel. authorities' approval 1 15MAY08 1 2 2			02AL	87	
Obtain design (DDA) approval from the SO 0 16SEP08 2 105 DDA submission for rel. authorities' approval 1 17SEP08 1 86 Design (DDA) review by the rel. authorities' approval for DDA 1 16OCT08 1 85 Obtain rel. authorities's approval for DDA 0 17OCT08 2 105 essment on WSD Tail Lam Chung WT No. 3 0 17OCT08 2 107 Design preparation for the AIP submission 30 08FEB08 08MAR08 2 3 Design (AIP) certification by the Design Checker 15 09MAR08 25 MAR08 2 3 Design (AIP) review by the SO's approval 1 25MAR08 25 MAR08 2 2 Design (AIP) review by the SO 0 26 MAR08 2 2 3 Obtain design (AIP) review by the SO 0 14 MAY08 2 2 Obtain design (AIP) authorities' approval from the SO 0 15 MAR08 1 2	i		16SEP08	105	
DDA submission for rel. authorities' approval 1 17SEP08 17SEP08 1 86 Design (DDA) review by the rel. authorities 28 18SEP08 1 50CT08 2 106 Obtain rel. authorities's approval for DDA 1 1 60CT08 1 85 1 60CT08 1 85 Obtain SO's consent for design (DDA) 0 170CT08 2 107 1 60CT08 1 60CT08 <td< th=""><th></th><th>0</th><th>P08</th><th>105</th><th>•</th></td<>		0	P08	105	•
Design (DDA) review by the rel. authorities 28 18SEP08 15OCT08 2 106 Obtain rel. authorities's approval for DDA 1 16OCT08 1 1 85 Obtain SO's consent for design (DDA) 0 17OCT08 2 107 essament on WSD Tal Lam Chung WT No. 3 30 08FEB08 08MAR08 2 3 Design preparation for the AIP submission for the SO's approval 1 25MAR08 23MAR08 3 8 Design (AIP) review by the SO 50 26MAR08 14MAY08 2 3 8 Dostign (AIP) review by the SO 0 26MAR08 14MAY08 2 2 4 Obtain design (AIP) approval from the SO 0 14MAY08 2 2 4 AIP submission for rel. authorities' approval 1 15MAY08 15 2 4		.	17SE	98	
Obtain rel. authorities's approval for DDA 1 16OCT08 16 COT08 1 Obtain SO's consent for design (DDA) 0 17OCT08 2 1 essment on WSD Tai Lam Chung WT No. 3 0 08FEB08 08MAR08 2 Design preparation for the AIP submission Design (AIP) certification by the Design Checker 15 09MAR08 23MAR08 2 Design (AIP) submission for the SO's approval 1 25MAR08 25MAR08 1 Design (AIP) review by the SO 0 14MAY08 2 Obtain design (AIP) approval from the SO 0 14MAY08 2 AIP submission for rel. authorities' approval 1 15MAY08 1			1500	106	
Obtain SO's consent for design (DDA) 0 17OCT08 2 10 essment on WSD Tai Lam Chung WT No. 3 30 08FEB08 08MAR08 2 10 Design preparation for the AIP submission 15 09MAR08 23MAR08 2 Design (AIP) certification by the Design Checker 15 09MAR08 23MAR08 1 Design (AIP) submission for the SO 50 26MAR08 1 2 Design (AIP) review by the SO 50 26MAR08 1 2 Obtain design (AIP) approval from the SO 0 14MAY08 2 AIP submission for rel. authorities' approval 1 15MAY08 1			9	82	
Bessment on WSD Tai Lam Chung WT No. 3 Design preparation for the AIP submission 30 08FEB08 08MAR08 2 Design (AIP) certification by the Design Checker 15 09MAR08 23MAR08 2 Design (AIP) submission for the SO 50 26MAR08 1 1 Design (AIP) review by the SO 50 26MAR08 1 2 Obtain design (AIP) approval from the SO 0 14MAY08 2 AIP submission for rel. authorities' approval 1 15MAY08 15MAY08 1	- 1	0	17OCT08 2	107	
Design preparation for the AIP submission 30 08FEB08 09MARN08 2 Design (AIP) certification by the Design Checker 15 09MAR08 23MAR08 2 Design (AIP) submission for the SO's approval 1 25MAR08 25MAR08 1 Design (AIP) review by the SO 50 26MAR08 14MAY08 2 Obtain design (AIP) approval from the SO 0 14MAY08 2 AIP submission for rel. authorities' approval 1 15MAY08 15MAY08 1	Impact Assessment on WSD Tai Lam Chung WT No. 3				
Design (AIP) certification by the Design Checker 15 09MAR08 23MAR08 2 Design (AIP) submission for the SO's approval 1 25MAR08 14MAY08 1 Design (AIP) review by the SO 50 26MAR08 14MAY08 2 Obtain design (AIP) approval from the SO 0 14MAY08 2 AIP submission for rel. authorities' approval 1 15MAY08 15MAY08 1		<u> </u>	-EB08 08MAR08 2	က	
Design (AIP) submission for the SO's approval 1 25MAR08 25MAR08 1 Design (AIP) review by the SO 50 26MAR08 14MAY08 2 Obtain design (AIP) approval from the SO 0 14MAY08 2 AIP submission for rel. authorities' approval 1 15MAY08 1			R08	က	
Design (AIP) review by the SO 50 26MAR08 14MAY08 2 Obtain design (AIP) approval from the SO 0 14MAY08 2 AIP submission for rel. authorities' approval 1 15MAY08 1 5MAY08 1			R08	ત્ય	
Obtain design (AIP) approval from the SO 0 14MAY08 2 AIP submission for rel. authorities' approval 1 15MAY08 15MAY08 1		\neg	, 708	CV	
AIP submission for rel. authorities' approval	i	0	708	2	•
		-	15MA	N	

Ingration of the Company Administration Description	ONG EARY CALTON DIFFMANTANSONSUPMANTANSONSUPMANTANSONSUPPARTIES SONSUPPARTIES SONSUPPA	PUD CONTRACTOR AND A SECOND CONTRACTOR OF THE
02L1FF0314 Design (AIP) review by the rel. authorities	28 16MAY08 12JUN08 2 3	
-	- :	
	14JUN08	
	23MAY08 21JUN08 2	
	06JUL08 2	
	07JUL08 07JUL08 1 3	
	50 08JUL08 26AUG08 2 3	
02L1FF0328 Obtain design (DDA) approval from the SO	0 26AUG08 2 3 •	
02L1FF0330 DDA submission for rel. authorities' approval	1 27AUG08 27AUG08 1 3	
	28 28AUG08 24SEP08 2 4	
	1 25SEP08 25SEP08 1 3	
02L1FF0336 Obtain SO's consent for design (DDA)	0 26SEP08 2 5	
Impact Assessment on KCRC West Rail Tunnel		
02L1FF0402 Design preparation for the AIP submission	30 08APH08 07MAY08 2 190	
02L1FF0404 Design (AIP) certification by the Design Checker	15 08MAY08 22MAY08 2 190	
02L1FF0406 Design (AIP) submission for the SO's approval	1 23MAY08 23MAY08 1 158	
02L1FF0408 Design (AIP) review by the SO	60 24MAY08 22JUL08 2 191	
02L1FF0410 Obtain design (AIP) approval from the SO	0 22JUL08 2 191 �	
02L1FF0412 AIP submission for rel. authorities' approval	ļ	
02L1FF0414 Design (AIP) review by the rel. authorities	28 24JUL08 20AUG08 2 191	
02L1FF0416 Obtain rel. authorities's approval for AIP	21 AUG08	
02L1FF0418 Obtain SO's consent for design (AIP)	0 22AUG08 2 192 🌄	- 1
02L1FF0420 Design preparation for the DDA submission	30 31JUL08 29AUG08 2 192	
02L1FF0422 Design (DDA) certification by the Design Checker	15 30AUG08 13SEP08 2 192	
02L1FF0424 Design (DDA) submission for the SO's approval	1 16SEP08 16SEP08 1 155	
102\L1FF0426 Design (DDA) review by the SO	60 17SEP08 15NOV08 2 190	
102L1FF0428 Obtain design (DDA) approval from the SO	0 15NOV08 · 2 190	
02L1FF0430 DDA submission for rel. authorities' approval	1 17NOV08 17NOV08 1 150	
02L1FF0432 Design (DDA) review by the rel. authorities	28 18NOV08 15DEC08 2 189	
	-	
02L1FF0436 Obtain SO's consent for design (DDA)	0 17DEC08 2 189	The state of the s
Impact Assessment on WSD Tsuen Wan Reservoir G.		
02L1FF0502 Design preparation for the AIP submission		
	21JUN08	
	1 23JUN08 23JUN08 1 205	
02L1FF0508 Design (AIP) review by the SO	60 24JUN08 22AUG08 2 250	
02L1FF0510 Obtain design (AIP) approval from the SO	0 22AUG08 2 250	
ı	1 23AUG08 23AUG08 1 201	
02L1FF0514 Design (AIP) review by the rel. authorities	28 24AUG08 20SEP08 2 251	
	1 22SEP08 22SEP08 1 200	
	23SEP08 2 251	
02L1FF0520 Design preparation for the DDA submission	30 015EP08 305EP08 2 251	

(

(

Activity Description	Grig Early Car Train DEFINAMENTS ON DEFINAMENTS ON DEFINAMENT OF THE PROPERTY	SOND, FMAMULIASIONDUFWAMELIASIO
02L1FF0522 Design (DDA) certification by the Design Checker	8 150CT08 2	1111 111 111 111 111 111 111 111 111 1
02L1FF0524 Design (DDA) submission for the SO's approval	1 16OCT08 16OCT08 1 202	
02L1FF0526 Design (DDA) review by the SO	60 17OCT08 15DEC08 2 251	
- 1	2	
- 1	16DEC08 1	
	17DEC08 13JAN09 2	
- !	14JAN09 14JA	
UZELIFFUSSE Uptain SUS consent for design (UUA)	0 15JAN09 2 251	
Design Packages Io. Wolls in Portion A		
Temp. Steel Decking Design Over Shing Mun Nullah		
02L1AA0102 Design preparation by the Designer	N.	-
i	-	
	28 08MAR08 04APR08 2 29 E	
02L1AA0110 Obtain design approval from the SO	0 04APR08 2 29	
ELS Design for Spiral Ramp/Cascade/Box Culvert		
02L1AA0202 Design preparation for the AIP submission	15 22FEB08 07MAR08 2 22 8	
02L1AA0204 Design (AIP) certification by the Design Checker	15 08MAR08 22MAR08 2 22 R	
02L1AA0206 Design (AIP) submission for the SO's approval		
02L1AA0208 Design (AIP) review by the SO	21 26MAR08 15APR08 2 20 🕸	
	0 15APR08 2 20	-
02L1AA0212 AIP submission for rel. authorities' approval	-	
02L1AA0214 Design (AIP) review by the rel. authorities	21 17APR08 07MAY08 2 20	
02L1AA0216 Obtain rel. authorities's approval for AIP	1 08MAY08 08MAY08 1 16	
02L1AA0218 Obtain SO's consent for design (AIP)	0 09MAY08 2 20	
02L1AA0220 Design preparation for the DDA submission	30 17APR08 16MAY08 2 20 協國	
02L1AA0222 Design (DDA) certification by the Design Checker	15 17MAY08 31MAY08 2 20 H	
02L1AA0226 Design (DDA) submission for the SO's approval	1 02JUN08 02JUN08 1 16	
1	2	
- 1	N08 2	
- !	24JUN08	
- 1	21 25JUN08 15JUL08 2 20	
	16JUL08 16JU	
02L1AA0238 Obtain SO's consent for design (DDA)	0 17JUL08 2 20 🗢	
Temp. Platform Design for H-Piling		
	R08 2	
	R08 2 1	
02L1AA0306 Design submission for the SO's approval	1 25MAR08 25MAR08 1 1,312	
02L1AA0308 Design review by the SO	28 26MAR08 22APR08 2 1,616 🔝	
Cascade & Box Culver Design for Portion A		
021.1AA0402 Design preparation for the AIP submission	30 08MAR08 06APR08 2 627	

20JUN08 2 23JUN08 21JUN08 1 22JUN08 21JUN08 1 22JUN08 21JUN08 1 16JUL08 30JUL08 2 31JUL08 30JUL08 2 31JUL08 30JUL08 2 29OCT08 29OCT08 2 21AJC08 29OCT08 2 20JUL08 20SEP08 1	建筑路梯	Original Early Cal Total Distriction of the Research Call Call Call Call Call Call Call Cal
Design (AP) review by the rel. authorities approval 1 ≥ 1,010NB Σ1,010NB 2 ≤ 1,010NB 2 ≤ 1,010NB 2 ≤ 1,010NB 2 ≤ 1,010NB 2 ≤ 25 6 6 6 6 6 6 6 7 6 7 7 7 7 7 7 7 8 8 8 8 8 8 8 8 8 8 9 8 9 8 9 8 9 8 9 8 9 8 9 8 9 9 9 9 9 9 9 9 9 9 9 9 9 1 0 1 0 1 0 1 0 1 0	-T	20JUN08 2
Obesign (MP) review by the rel. authorities 15 22JUNG 60.01.U.08 2 25 Obtain SO's consent for design (MP) review by the rel. authorities 1 07JULG 6 07JULG 8 2 25 Obesign (DA) designation by the Design Checker 1 07JULG 8 02JULG 8 2 25 Design (DA) review by the SO approval for mine SO 0 0 07JULG 8 2 25 Design (DA) review by the SO approval for DA 1 00JULG 8 2 25 Obesign (DA) review by the rel. authorities 2 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	T	21JUN08 21JUN08 1
Obasin Class approval for AlP 1 07.ULL06 07.ULL08 2 Cibain SCS consent for design (AlP) 0 06.ULL08 2 25 Design Clobal centification by the Design Checker 15 16.UND8 15.ULL08 2 25 Design (DDA) centification by the Design Checker 15 16.ULN08 15.ULL08 2 25 Design (DDA) centification by the Design Checker 15 16.ULN08 15.ULL08 2 25 Design (DDA) centification by the Design Checker 16 17.ULC08 2 25 Design (DDA) centification by the Design Checker 17 20.0CTO8 2 25 Design (DDA) centification by the Design Checker 15 20.0CTO8 2 25 Design (DA) center of the SO's approval 1 20.0CTO8 2 25 Oth Chain SC's consent for design (DDA) 1 20.0CTO8 2 25 Obesign (ALP) centification by the Design Checker 15 21.UNO8 2 28 Obesign (ALP) centification by the Design Checker 15 21.UNO8 2	- 1	22JUN08 06JUL08 2
Design (DA) submission for the SOT supproval of 1 1 31.0 10	- 1	07JUL08 07JUL08 1
Design (DDA) submission of the DA submission 30 Isial lung isial lung 15 il lung 2 En Il lung 3 EN Il lung	-1	08JUL08 2
Design (DDA) certification by the Design Checker 15 16JUL06 30JUL06 2 25		16JUN08 15JUL08 2
Design (DDA) submission for the SO's approval 1 31.41L08 31.41L08 1 21 Design (DDA) submission for the SO's approval 0 0 14.408 2385EP08 2 55 DAS above (SAS) approval from the SO 0 0 14.408 2385EP08 2 55 DAS authorities approval from the SO 0 0 17.408 20.507T08 2 50 Obtain cleasing (DDA) approval from the SO 1 20.507T08 2 50 2 56 Obtain cleasing (DDA) approval from the SO 1 20.507T08 2 50 2 56 Obtain Cleasing (DDA) approval from the SO 1 20.507T08 2 57 2 57 Design (API) review by the ref. authorities approval from the SO's approval	†	16JUL08 30JUL08 2
Design (DA) review by the SO	_	31JUL08 31JUL08 1
Obtain design (DDA) approval from the SO Obtain design (DDA) as unthinties approval a troub and submission for ela authorities approval a troub and the submission for tela authorities approval a troub and the submission for tela authorities approval a secondary and the submission for tela authorities approval and the submission for the SOs approval and the submission for the SOs approval from the SOS approval and the submission for the submis	ĵ	01AUG08 29SEP08 2
DDA submission for rel. authorities approval 1 30SEP08 30SEP08 1 28		29SEP08 2
Design (DDA) review by the rel, authorities 28 010CT08 280CT08 2 26 Obtain rel, authorities's approval for DDA 290CT08 2 26 Obtain rel, authorities's approval for DDA 2 20CT08 2 26 Obtain rel, authorities's approval for DDA 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2		30SEP08 1
Obtain rel, authorities's approval for DDA 1 290CT08 290CT08 2 26	- 1	01OCT08 28OCT08 2
Obtain SO's consent for design (DDA)	ŧ	29OCT08
Design preparation for the AIP submission 30 21APR08 20MAY08 2 527 182	- 1	
Design preparation for the AIP submission 30 21APR08 20MAY08 2 557 Em Design (AIP) certification by the Design Checker 15 21MAY08 0.4UN08 2 804 1 652UN08 1 653 1 Em 1 1 0.5UN08 0.5UN08 1 652 804 1 1 0.5UN08 0.5UN08 1 652 804 1 1 0.5UN08 0.5UN08 0.5UN08 1 652 804 1 1 0.5UN08 1 1 0.5UN08 1 1 0.5UN08 1 652 804 1 1 0.5UN08 1 <	Temp. Support Design for MA and MA/MT Connection	
Design (AIP) certification by the Design Checker 15 21MAY08 04JUN08 2 804 Design (AIP) submission for the SO's approval 1 05JUN08 05JUN08 1 653 Obtain design (AIP) review by the SO 0 0 04AUG08 2 804 AIP submission for ret. authorities a paproval from the SO 0 0 05AUG08 1 652 Design (AIP) review by the ret. authorities a paproval from the SO 0 0 2AUG08 2 804 Design (AIP) review by the ret. authorities a paproval from the SO 0 1 21AUG08 2.2AUG08 2 804 Obtain SO's consent for design (AIP) 0 21AUG08 2.8AUG08 2 804 Design (DDA) certification by the Design Checker 1 1.6SEP08 1.5SEP08 1.652 Design (DDA) serview by the sol 0 1.7TNOV08 1.7NOV08 1.7NOV08 2.803 Design (DDA) review by the ret. authorities approval 1 1.6DEC08 2 803 Dbsign (DDA) review by the ret. authorities approval 1 1.7NOV08 <th>02L1BB0602 Design preparation for the AIP submission</th> <th>21APR08 20MAY08 2</th>	02L1BB0602 Design preparation for the AIP submission	21APR08 20MAY08 2
Design (AIP) submission for the SO's approval		21MAY08 04JUN08 2 804
Design (AIP) review by the SO 60 GBJUN0B 04AUG0B 2 804 AIP submission for ref. authorities' approval from the SO 0 GAUG0B 2 804 AIP submission for ref. authorities' approval from the SO 1 GAUG0B 2 804 AIP submission for ref. authorities' approval from the SO 1 CAUG0B 2 AUG0B 1 GE2 Design (AIP) review by the ref. authorities 1 21AUG0B 21AUG0B 2 804 Design (AIP) review by the SO 3 1JUL0B 22AUG0B 2 804 Design (DDA) certification by the Design Checker 15 30AUG0B 2 803 Design (DDA) certification by the Design Checker 15 30AUG0B 2 803 Design (DDA) submission for the SO's approval 1 16SEP0B 15NOV0B 2 803 Design (DDA) review by the SO 0 17NOV0B 1 GE1 Design (DDA) review by the SO 0 17NOV0B 1 GE1 Design (DDA) review by the ref. authorities 2 800 DDA submission for ref. authorities 3 PUROV0B 1 TOROV0B 2 803 DDA submission for ref. authorities 3 PUROV0B 1 TOROV0B 2 803 Design (DDA) review by the SO 0 1 TOROV0B 2 803 Design (DDA) review by the Design Checker 15 20JIN0B 2 730 Design for MAAMAS/NDS/DC/AVS 2 803 Design (AIP) review by the SO 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 0 Design (AIP) review by the Rol authorities 0 SEEP0B 0		05JUN08 05JUN08 1 653
Obtain design (AIP) approval from the SO 0 04AUG08 2 804 AIP submission for ret. authorities' approval 1 05AUG08 05AUG08 1 652 Design (AIP) review by the rel. authorities approval for AIP 1 21AUG08 1 652 Obtain SO's consent for design (AIP) 0 22AUG08 2 804 Design (DDA) review by the DDA submission 1 16SEP08 15SEP08 1 652 Design (DDA) certification by the Design Checker 15 30AUG08 1 652 Design (DDA) review by the SO 0 17SEP08 15NOV08 1 651 Design (DDA) review by the SO 0 17SEP08 1 651 Design (DDA) review by the CL authorities approval 1 16DEC08 1 651 Design (DDA) review by the CL authorities approval 1 16DEC08 1 648 Obtain GO's consent for design (DDA) 0 17DEC08 2 803 Design (DDA) review by the CL authorities approval 1 16DEC08 1 648 Obtain GO's consent for design (DDA) 0 17DEC08 2 803 Design for MAA/MAS/VDS/CC/AVS 0 17DEC08 2 803 Design for MAA/MAS/VDS/CC/AVS 0 0 17DEC08 2 803 Design (AIP) review by the SO 0 0 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 0 0 Design (AIP) review by the SO 0 0 0 0 0 0 Design (AIP) review by the CO 0 0 0 0 0 0 Design (AIP) review by the CO 0 0 0 0 0 0 0 Design (AIP) review by the CO 0 0 0 0 0 0 0 Design (AIP) review by the rel. authorities approval from the SO 0 0 0 0 0 0 0 0 0 Design (AIP) review by the rel. authorities approval from the SO 0 0 0 0 0 0 0 0 0	j	06JUN08 04AUG08 2 804
AlP submission for ref. authorities approval 1 05AUG08 05AUG08 1 662 Design (AIP) review by the ref. authorities 15 06AUG08 2 AUG08 2 804 Obtain SO's consent for design (AIP) 0 21AUG08 2 AUG08 2 804 Design preparation for the DDA submission 30 31JUL08 23AUG08 2 804 Design (DDA) certification by the Design Checker 15 30AUG08 2 804 Design (DDA) certification by the Design Checker 15 30AUG08 2 803 Design (DDA) submission for the SO's approval 1 15SEP08 15ESEP08 1 651 Design (DDA) review by the SO 0 17NOV08 1 803 803 DDA submission for rel. authorities's approval for DDA 1 17NOV08 1 661 17DEC08 2 803 Obtain rel. authorities's approval for DDA 1 1 1 17DEC08 2 803 Obtain rel. authorities's approval for the SO's consent for design (DDA) review by the SO 60 06	1	04AUG08 2 804
Design (AIP) review by the rel. authorities 15 06AUG08 ZOAUG08 2 804 Obtain rel. authorities's approval for AIP 1 21AUG08 21AUG08 1 652 Obtain SO's consent for design (AIP) 0 22AUG08 2 804 Design preparation for the DDA submission 30 31JUL08 29AUG08 2 804 Design (DDA) certification by the Design Checker 15 30AUG08 1 652 803 Design (DDA) review by the SO 60 17SEP08 15NOV08 2 803 Obtain design (DDA) review by the rel. authorities' approval from the SO 0 17NOV08 1 648 Design (DDA) review by the rel. authorities' approval for DDA 1 17NOV08 1 648 Obtain Gos or sent for design (DDA) 0 17DEC08 2 803 Design for MAAMAS/VDS/DC/AVS 1 16DEC08 2 803 Design for MAAMAS/VDS/DC/AVS 2 2 20JUN08 2 2 Design (AIP) submission for the AIP submission for the SO 0		05AUG08 05AUG08 1
Obtain SO's consent for design (AIP) 1 21AUG08 1 652 Obtain SO's consent for design (AIP) 0 22AUG08 2 804 Design preparation for the DDA submission 30 31JUL08 29AUG08 2 804 Design (DDA) certification by the Design Checker 15 30AUG08 185EP08 1 652 Design (DDA) submission for the SO's approval 1 16SEP08 16SEP08 1 651 Design (DDA) review by the SO 0 17NOV08 2 803 DDA submission for rel. authorities' approval from the SO 0 17NOV08 1 651 DDA submission for rel. authorities' approval for DDA 1 1 17NOV08 1 648 Obtain As So consent for design (DDA) 0 1 1 1 648 648 Obtain SO's consent for design (DDA) 0 1 1 1 648 648 Obtain SO's consent for design (DDA) 0 1 1 1 648 648 Design (AIP) certification by the Design		06AUG08 20AUG08 2
Obtain SO's consent for design (AIP) 0 22AUG08 2 804 Design preparation for the DDA submission 30 31JUL08 22AUG08 2 804 Design (DDA) certification by the Design Checker 15 30AUG08 1 652 803 Design (DDA) submission for the SO's approval 60 17SEP08 1 652 803 Obtain design (DDA) review by the SO 0 1 15NOV08 2 803 Obtain design (DDA) review by the rel. authorities approval from the SO 0 1 1NOV08 1 648 Obtain rel. authorities s approval for DDA 1 1 6DEC08 1 648 Obtain SO's consent for design (DDA) 0 2 1MAY08 2 803 Obtain SO's consent for design (DDA) 0 2 1MAY08 2 300 Design for MAAMAS/VDS/DCAVS 1 1 6DEC08 1 591 Design (AIP) certification by the Design Checker 15 20JUL08 2 730 Design (AIP) review by the SO 60 0 60 0 3SEP08 2 730 Obtain design (AIP) review by the rel. authorities 1 0 65EP08 1 592		21AUG08 21AUG08 1
Design preparation for the DDA submission 30 31 JUL08 29AUG08 2 804 Design (DDA) certification by the Design Checker 15 30AUG08 13SEP08 1 652 Design (DDA) submission for the SO's approval 60 17SEP08 16SEP08 1 652 Design (DDA) review by the SO 0 17SEP08 15NOV08 2 803 DDA submission for rel. authorities' approval from the SO 0 17NOV08 17NOV08 1 648 DDA submission for rel. authorities' approval from the SO 0 17NOV08 1 648 DDA submission for rel. authorities' approval for DDA 1 1 17NOV08 1 648 Obtain SO's consent for design (DDA) 0 1 1 1 648 68 Design for MAAMAS/NDS/DC/AVS 1 1 1 1 1 1 1 1 1 Design (AIP) review by the SO 0 0 1 1 2 3 1 1 1 1 1 1 <		22AUG08 2
Design (DDA) certification by the Design Checker 15 30AUG08 13SEP08 2 804 Design (DDA) submission for the SO's approval 1 16SEP08 1 652 803 Obtain design (DDA) review by the SO 0 0 15NOV08 2 803 Obtain design (DDA) review by the rel. authorities' approval from the SO 1 17NOV08 1 661 Design (DDA) review by the rel. authorities' approval for DDA 1 17NOV08 1 661 Obtain rel. authorities' approval for DDA 1 16DEC08 1 648 Obtain SOs consent for design (DDA) 0 1 17DEC08 2 803 Design for MAAMAS/VDS/DC/AVS 1 1 16DEC08 1 643 1 17DEC08 2 2 803 Design for MAAMAS/VDS/DC/AVS 1 1 1 17DEC08 2 2 2 2 2 2 2 2 2 2 1 1 1 1 1 1 1 1 1		31JUL08 29AUG08 2 804
Design (DDA) submission for the SO's approval Design (DDA) review by the SO 60 17SEP08 16SEP08 1 652 653 654 655 654 655 654 655 654 655 654		30AUG08 13SEP08 2 804
Design (DDA) review by the SO 60 17SEP08 15NOV08 2 803 Obtain design (DDA) approval from the SO 0 15NOV08 2 803 DDA submission for rel. authorities' approval for DDA 1 17NOV08 1 651 Design (DDA) review by the rel. authorities approval for DDA 1 16DEC08 2 802 Obtain rel. authorities's approval for DDA 0 1 17DEC08 2 803 Design (DDA) review by the rel. authorities of consent for design (DDA) 0 1 17DEC08 2 802 Design for MAA/MAS/VDS/DC/AVS 0 1 17DEC08 2 803 Design for INDA AMAS/VDS/DC/AVS 30 21MAY08 19JUN08 2 730 Design for INDA AMAS/VDS/DC/AVS 1 60 06JUL08 05JUL08 2 730 Design (AIP) review by the SO 60 06JUL08 04JUL08 2 730 AIP submission for rel. authorities approval 1 04SEP08 2 730 Design (AIP) review by the rel. authorities approval		16SEP08 16SEP08 1
Obtain design (DDA) approval from the SO 0 15NOV08 2 803 DDA submission for rel. authorities' approval 1 17NOV08 1 651 Design (DDA) review by the rel. authorities' approval for DDA 1 16DEC08 2 802 Obtain SO's consent for design (DDA) 0 17DEC08 2 803 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 19JUN08 2 527 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 19JUN08 2 730 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 19JUN08 2 730 Design (AIP) review by the SO besign Checker 15 20JUL08 05JUL08 2 730 Obtain design (AIP) review by the SO besign (AIP) review by the rel. authorities' approval 1 04SEP08 2 730 AIP submission for rel. authorities' approval 1 04SEP08 2 730 Design (AIP) review by the rel. authorities 1 05SEP08 2 730 Design (AIP) review by the rel. authorities 1 05SEP08	1	17SEP08 15NOV08 2
DDA submission for rel. authorities' approval 1 17NOV08 1 651 Design (DDA) review by the rel. authorities 28 18NOV08 15DEC08 2 802 Obtain rel. authorities's approval for DDA) 0 17DEC08 2 803 Design (DDA) review by the rel. authorities' approval 30 21MAY08 17DEC08 2 803 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 19JUN08 2 527 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 19JUN08 2 730 Design for MAA/MAS/VDS/DC/AVS 15 20JUN08 04JUL08 2 730 Design (AIP) review by the SO 60 06JUL08 03SEP08 2 730 AIP submission for rel. authorities' approval from the SO 0 0 03SEP08 2 730 AIP submission for rel. authorities' approval for AIP 1 04SEP08 2 730 Design (AIP) review by the rel. authorities 1 05SEP08 2 730 Design (AIP) review by the rel. authorities' approval for AIP <th></th> <th>15NOV08 2</th>		15NOV08 2
Design (DDA) review by the rel. authorities 28 18NOV08 15DEC08 2 802 Obtain rel. authorities's approval for DDA 1 16DEC08 1 648 Obtain SO's consent for design (DDA) 0 17DEC08 2 803 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 19JUN08 2 527 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 19JUN08 2 730 Design for MAA/MAS/VDS/DC/AVS 15 20JUN08 2 730 Design for MAA/MAS/VDS/DC/AVS 1 05JUL08 2 730 Design (AIP) review by the SO 60 05JUL08 2 730 AIP submission for rel. authorities' approval from the SO 0 0 03SEP08 2 730 AIP submission for rel. authorities' approval 1 04SEP08 2 730 Design (AIP) review by the rel. authorities' approval for AIP 1 05SEP08 2 730 Design (AIP) review by the rel. authorities' approval for AIP 1 20SEP08 1 592 <th>- 1</th> <th>17NOV08 17NOV08 1</th>	- 1	17NOV08 17NOV08 1
Obtain rel. authorities's approval for DDA 1 16DEC08 1 648 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 2 803 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 2 730 Design for Paration or the AIP submission for the SO's approval 1 20JUL08 2 730 Design (AIP) review by the SO 60 06JUL08 03SEP08 2 730 AIP submission for rel. authorities' approval from the SO 0 03SEP08 2 730 AIP submission for rel. authorities' approval from the SO 1 04SEP08 2 730 Design (AIP) review by the rel. authorities' approval for AIP 1 04SEP08 2 730 Design (AIP) review by the rel. authorities' approval for AIP 1 04SEP08 2 730		18NOV08 15DEC08 2
Design for MAA/MAS/VDS/DC/AVS 0 17DEC08 2 803 Design for MAA/MAS/VDS/DC/AVS 30 21MAY08 2 527 Design preparation for the AIP submission Design (AIP) certification by the Design Checker 15 20/UN08 2 730 Design (AIP) review by the SO 60 06JUL08 03SEP08 2 730 Obtain design (AIP) review by the rel. authorities' approval from the SO 0 03SEP08 2 730 AIP submission for rel. authorities' approval from the SO 1 04SEP08 1 592 Design (AIP) review by the rel. authorities' approval for AIP 1 04SEP08 2 730 Design (AIP) review by the rel. authorities' approval for AIP 1 20SEP08 1 592	- 1	16DEC08 1
Design for MAA/MAS/VDS/DC/AVS 21 MAYOB 2 527 EE Design reparation for the AIP submission 30 21 MAYOB 2 527 730 Design (AIP) certification by the Design Checker 15 20JUNOB 2 730 730 Design (AIP) submission for the SO's approval 1 05JULOB 05JULOB 2 730 Obtain design (AIP) review by the SO 0 06JULOB 2 730 AIP submission for rel. authorities' approval 1 04SEPOB 2 730 AIP submission for rel. authorities' approval 1 04SEPOB 1 592 Design (AIP) review by the rel. authorities 15 05SEPOB 1 592		17DEC08 2
Design preparation for the AIP submission 30 21MAY08 19JUN08 2 527 Design (AIP) certification by the Design Checker 15 20JUN08 04JU108 2 730 Design (AIP) submission for the SO's approval 1 05JUL08 1 591 Obtain design (AIP) review by the SO 0 05JUL08 2 730 AIP submission for rel. authorities' approval 1 04SEP08 2 730 AIP submission for rel. authorities 1 04SEP08 1 592 Design (AIP) review by the rel. authorities 15 05SEP08 19SEP08 2 730 Obtain rel. authorities's approval for AIP 1 20SEP08 1 592	ш:	
Design (AIP) certification by the Design Checker 15 Z0JUN08 04JUL08 2 730 Design (AIP) submission for the SO's approval 60 06JUL08 05JUL08 1 591 Obtain design (AIP) review by the SO 0 0 03SEP08 2 730 AIP submission for rel authorities' approval 1 04SEP08 0 730 Design (AIP) review by the rel. authorities 15 05SEP08 1 592 Design (AIP) review by the rel. authorities 1 04SEP08 2 730 Obtain rel. authorities's approval for AIP 1 20SEP08 1 592		21MAY08 19JUN08 2
Design (AIP) submission for the SO's approval 1 05JUL08 05JUL08 1 Design (AIP) review by the SO 60 06JUL08 2 2 Obtain design (AIP) approval from the SO 0 03SEP08 2 AIP submission for rel. authorities' approval 1 04SEP08 04SEP08 1 Design (AIP) review by the rel. authorities 15 05SEP08 1 20SEP08 2 Obtain rel. authorities's approval for AIP 1 20SEP08 20SEP08 1		20JUN08 04JUL08 2 730
Design (AIP) review by the SO 60 06JUL08 03SEP08 2 Obtain design (AIP) approval from the SO 0 03SEP08 2 AIP submission for rel. authorities' approval 1 04SEP08 04SEP08 1 Design (AIP) review by the rel. authorities 15 05SEP08 19SEP08 2 Obtain rel. authorities's approval for AIP 1 20SEP08 20SEP08 1		05JUL08 05JUL08 1
Obtain design (AIP) approval from the SO 0 03SEP08 2 AIP submission for rel. authorities' approval 1 04SEP08 04SEP08 1 Design (AIP) review by the rel. authorities 15 05SEP08 19SEP08 2 Obtain rel. authorities's approval for AIP 1 20SEP08 20SEP08 1	i	06JUL08 03SEP08 2
AIP submission for rel. authorities' approval 1 04SEP08 1 04SEP08 1 Design (AIP) review by the rel. authorities 15 05SEP08 19SEP08 2 Obtain rel. authorities's approval for AIP 1 20SEP08 20SEP08 1	-	03SEP08 2
Design (AIP) review by the rel. authorities 15 05SEP08 19SEP08 2 Obtain rel. authorities's approval for AIP 1 20SEP08 20SEP08 1		04SEP08 04SEP08 1
Obtain rel. authorities's approval for AIP 1 20SEP08 20SEP08 1	ì	05SEP08 19SEP08 2
		20SEP08 20SEP08 1

Weindige Description	Ong Early Die Stat	Early Cal	Total DIT FINANTS	B STATE OF THE STATE OF STATE	2012
02L1BB0718 Obtain SO's consent for design (AIP)		EP08	729	4.15.18171.8179.202.1222.722.4252.722.2333.132333333333333334.04.1.424.34.445.18.7.4833031.12.2334155.6	568758598081626384858
1	30 31AUG08	29SEP08 2	729		
	15 30SEP08	14OCT08	729	\$25	
-r	1 15OCT08	15OCT08 1	592		
i	60 16OCT08	14DEC08 2	729		
021 1880/28 Obtain design (DDA) approval from the SO		14DEC08 2	729		
1001 1880739 Design (DDA) review by the collection	-+-	15DEC08 1	591		
"	28 16DECU8	12.JAN09 2	729		-8441-
02L1BB0736 Obtain SO's consent for design (DDA)	0	14JAN09 2	729		
	30 20JUN08	19JUL08 2	527		
	15 20JUL08	03AUG08 2			
	1 04AUG08	04AUG08 1	429		
	60 05AUG08	03OCT08 2	527		
	0	03OCT08 2	527	•	
	1 04OCT08	04OCT08 1	427		
	15 05OCT08	19OCT08 2	527	E22	
02L1BB0816 Obtain rel. authorities's approval for AIP	1 20OCT08	20OCT08 1	429		
02L1BB0818 Obtain SO's consent for design (AIP)	0	210CT08 2	531		
02L1BB0820 Design preparation for the DDA submission	30 29SEP08	-	531		
	15 29OCT08	ļ	531		-,
	1 13NOV08 13NOV08	13NOV08	428		
_	60 14NOV08 12JAN09	12JAN09 2	531		
02L1BB0828 Obtain design (DDA) approval from the SO	0	12JAN09 2	531	•	
	1 13JAN09	13JAN09 1	428		
- 1	14JAN09	10FEB09 2	531		
- 1	1 11FEB09 : 11FE	11FEB09 1	430		
02L1BB0836 Obtain SO's consent for design (DDA)	0	12FEB09 2	531	•	
%					
- 1	15 06APR08 20AP	20APR08 2	50		
- 1	15 21APR08 05MAY08	05MAY08 2	20		
i	1 06MAY08	06MAY08 1	41		
ļ	21 07MAY08 27MA	27MAY08 2			
	0	27MAY08 2			
02L1BB0912 AIP submission for rel. authorities' approval	1 28MAY08 28MAY08	ļ.,			
Ļ	28 29MAY08	25JUN08 2	20		
- 1	1 26JUN08	26JUN08 1			
	0	27JUN08 2			
	30 05JUN08	04JUL08 2			
	15 05JUL08	19JUL08 2	20		*******
02L18B0924 Design (DDA) submission for the SO's approval	1 21JUL08	21JUL08 1	42		

-

io	Early Cal Total	The second of the second
133	DUT. Start Firsh ID Float Public Association of Association of Association of Association and Associ	EMATRUTA SOL
	2 49	BF75B596061626364656
7	0 11AUG08 2 49	
T	-	
	2	
Т	1 10SEP08 10SEP08 1 40	
02L1BB0936 Obtain SO's consent for design (DDA)	0 11SEP08 2 50	
िस्टीम् मार्गात्रका हुन् हुन्ता अस्ति अस्ति मार्गाहरू		
ELS Design for Intake Structure Construction		
02L1CC0102 Design preparation by the Designer	15 08FEB08 22FEB08 2 301 B	
02L1CC0104 Design certification by the Design Checker	15 23FEB08 08MAR08 2 30	
	2 2	
02L1CC0108 Design review by the SO	·	
02L1CC0110 Obtain design approval from the SO	2	
Temp. Support Design for MAA/MAS/VDS/DC/AVS		-
02L1CC0302 Design preparation for the AIP submission	30 09MAR08 07APR08 2 262	
	2 262	
- 1	-	
- 1	22JUN08 2	
	22JUN08 2	
-	1 215	
	15 24JUN08 08JUL08 2 262	
	-	
	2 263	
1	30 18JUN08 17JUL08 2 263 🖼	
	<u>!</u> 	
- 1	1 02AUG08 02AUG08 1 212	
	60 03AUG08 01OCT08 2 263	
	0 010CT08 2 263	
	1 02OCT08 02OCT08 1 211	·
02L1CC0332 Design (DDA) review by the rel. authorities	28 03OCT08 2 263	
02L1CC0334 Obtain rel. authorities's approval for DDA	1 310CT08 310CT08 1 211	
02L1CC0336 Obtain SO's consent for design (DDA)	0 01NOV08 2 263	
Temp. Support Design for MA and MA/MT Connection		
	30 08MAY08 06JUN08 2 395 E	
i	15 07JUN08 2 395	
02L1CC0406 Design (AIP) submission for the SO's approval	8 1	
i	2	
	2	
i	1 23AUG08 23AUG08 1 320	
	2	
	1 08SEP08 08SEP08 1 319	·
02L1CC0418 Obtain SO's consent for design (AIP)	0 09SEP08 2 394	
	Chane 10 A 17	

nnission 30 18AUG08 ISEED08 2 394 O'S approval 15 17SEP08 01.0EC08 2 394 O'S approval 1 020CT08 01.0EC08 2 394 Irle SO 0 030CT08 01.0EC08 2 394 Irle SO 0 0 01.0EC08 1 394 Irle SO 0 0 02.0CT08 01.0EC08 1 394 Irle SO 0 0 0 02.0EC08 1 394 394 Irle SO 0 0 0 0 0 0 394	The scription	Sing Early Car Total DEFINANT DASSESS OF STATE AND STATE OF STATE STATE OF
Design (DA) certification by the Design Cheacker 15 175EP08 010CTT08 2 394 Design (DA) submission for the SO's approval 1 020EC08 2 394 Design (DA) approval from the SO 6 6 030CT08 1 320 Design (DA) approval from the SO 6 030CT08 010EC08 2 394 Design (DA) approval from the SO 0 030CT08 010EC08 2 394 Design (DA) approval from the SO 0 030CT08 010EC08 2 394 Design (DA) average by the sol authorities approval from the SO 030CT08 010EC08 2 394 Design (DA) average by the sol authorities approval from the SO 030CT08 010EC08 2 394 Design (DA) average by the sol authorities approval from the SO 030CT08 010EC08 2 394 Design (AP) review by the sol authorities approval from the SO 030CT08 010EC08 2 286 Design (AP) review by the sol authorities approval from the SO 030CT08 010EC08 2 286 Design (AP) review by the sol authorities approval from the SO 030CT08 00CT08 00CT08 0 2 Design (AP) review by the sol authorities approval from the SO 00CT08 00CT08 0 2 2 2 Design (DA) certification by the Design Checker 15 034M/Y08 2 2 2 2 Design (DA) certification by the Design Checker 15 034M/Y08 0 2 2 2 2 Design (DA) certification by the Design Checker 15 034M/Y08 0 2 2 2 2 Design (DA) certification by the Design Checker 15 034M/Y08 0 2 2 2 2 Design (DA) certification by the Design Checker 15 034M/Y08 0 2 2 2 2 2 2 Design (DA) certification by the Design Checker 15 034M/Y08 0 2 2 2 2 2 2 2 2 2		18AUG08 16SEP08 2 394
Design (DA) submission for the SO's approval 1 (2000T08) (2000T08) (1 (2000T08) (2 (2000T08)		17SEP08 01OCT08 2 394
Design (DA) review by the SO		02OCT08 02OCT08 1
Obtain design (IDA) approval from the SO	- 1	03OCT08 01DEC08 2 394
Doba burnission for rel. authorities approval 1 ΩΣDECOR 319 Design (DDA) review by the rel. authorities 20 30DECOR 319 Obtain SO's consent for design (DDA) 1 31DECOR 310ECOR 2 Obtain SO's consent for design (DDA) 0 31DECOR 310ECOR 2 384 Design reparation for the API submission 30 6A-PRO 7 22A 384 Design (API) settlification by the Design Checker 15 31DEA/OR 2.22LULOR 2 285 Design (API) settlification by the Design Checker 15 22ALULOR 2.23LULOR 2 286 Alexandresion for the SOT sapproval 1 22ALULOR 2.23LULOR 2.285 Remanded Personal Personal For AIP 4 Obtain rel. authorities approval for the SOT sapproval 1 2.4LULOR 0.4ALUGOR 2.285 4 Design (DDA) review by the SOT 0 0.2ESEDOR 0 2.2BLULOR 2.285 8 Design (DDA) review by the SOT 0 0.2ESEDOR 0 0.2ALULOR 1.223 <t< th=""><th>— Ţ</th><th>01DEC08 · 2</th></t<>	— Ţ	01DEC08 · 2
Design (Abr) review by the ret, authorities approval for DDA, 0 0 0 0 0 0 0 0 0	7	02DEC08 02DEC08 1
Obtain ret, authorities's approval for DDA 1 31DECOB 31DECOB 1 32AND 2 35A Design for MAAAMASVDSCOCNOS 30 GRAPEOR 0.2AND 2 285 EST Design for MAAAMASVDSCOCNOS 30 GRAPEOR 0.0ANDAYOB 2 285 EST Design for MAAAMASVDSCOCNOS 30 0.0ANDAYOB 2.2AULOB 2 285 EST Design (AIP) submission for the SOS approval from the SO 0 2.2AULOB 2 286 Design (AIP) 1 1 2.2AULOB 2 286 Design (AIP) 1 1 2.2AULOB 2 286 Design (AIP) 2 286 Design (AIP) </th <th></th> <th>03DEC08 30DEC08 2</th>		03DEC08 30DEC08 2
Design for MAMASANSOLOGIANS 0 08APR08 07AMAYOS 2 285 FIRE Design for MAMASANSOLOGIANS 0 08APR08 07MAYOS 2 285 FIRE Design from the All Submission or the All Submission for the SO's approval 1 23MAYOS 22MAYOS 2 285 FIRE Obtain design (AIP) sertimetation by the Design Checker 1 22MAYOS 22JULOS 2 285 FIRE Obtain design (AIP) approval from the SO's approval from the SO 0 4MAYOS 22JULOS 2 285 FIRE Obtain design (AIP) review by the rel. authorities approval from the SO's approval from the SO's consent for design (AIP) 1 1 22JULOS 2 285 FIRE Design (DA) review by the rel. authorities approval from the SO's approval fro		31DEC08 31DEC08 1
Design for MAAMAS/USDCANS 30 08APR08 07MAY08 2.856 FER Design for Indexident on the ARD submission 1 20MAY08 22MAY08 2.826 FER Design (ARP) submission for the SO's approval 1 23MAY08 22MAY08 2.826 FER Design (ARP) submission for the SO's approval 1 22MAY08 22MAY08 2.856 FER AlP submission for rel, authorities approval for AR 1 23MAY08 2.24MAY08 2.856 FER AlP submission for rel, authorities approval for AR 1 23MAY08 2.24MAY08 2.856 FER Design (ARP) review by the rel: authorities approval for AR 1 3.24MAY08 2.24MAY08 2.856 FER Design (DA) review by the rel: authorities approval for AR 1 1.01MAY08 1.229 FER FER Design (DA) submission for the SO's approval 1 1.17ALIG08 2.81ALIG08 2.86 FER FER Design (DA) submission for the SO's approval from the SO's approval 1 1.01MOY08 1.229 EER FER Des		02JAN09 2
Design preparation for the AIP submission 30 GBAPR08 C 285 FB Design (AIP) carbitration by the Design Checker 15 60MAYOB 22 AMYOB 2 285 FB Design (AIP) submission for the SO's approval 1 23MAYOB 22 ALULOB 2 285 FB Obesign (AIP) submission for rel. authorities approval from the SO 0 44MAYOB 22JULOB 2 285 FB AIP submission for rel. authorities approval from the SO 0 24MAYOB 22JULOB 2 285 FB Obtain rel. authorities approval from the SO 0 24MLOB 2 24MLOB 2 286 FB Obtain rel. authorities approval for AIP 0 1 22JULOB 2 286 FB Obtain rel. authorities approval for AIP 0 1 2 24LUCOB 2 285 FB Design (DA) submission for the DA submission 0 0 2 286 COCTOB 2 286 <t< th=""><th></th><th></th></t<>		
Design (AIP) certification by the Design Checker 15 (98MAY08 (22MAY08 1 235) Design (AIP) setrification by the SOS approval 1 23MAY08 (22MAY08 1 228) Design (AIP) submission for the SOS approval 1 23MAY08 (22MAY08 1 228) AIP submission for rel, authorities approval from the SO (22MU.08 (22MU.08 1 228) AIP submission for rel, authorities approval for DA (AIP) (22MU.08 (22MU.08 1 228) Design (AIP) review by the rel, authorities approval for AIP (22MU.08 (22MU.08 1 228) Design (AIP) review by the rel, authorities approval for AIP (22MU.08 (22MU.08 1 228) Design (DDA) certification by the Design Checker 15 (77AU.08 (22MU.08 228) Design (DDA) certification by the Design Checker 15 (77AU.08 (22MU.08 228) Design (DDA) review by the rel, authorities approval for DDA (22MU.08 (22MU.08 22MU.08 228) Design (DDA) review by the rel, authorities approval for DDA (22MU.08 (22MU.08 22MU.08 22MU.08 (22MU.08 22MU.08 22MU.08 (22MU.08 22MU.08 22MU.08 22MU.08 (22MU.08 22MU.08 (22MU.08 22MU.08 (22MU.08 22MU.08 (22MU.08 22MU.08 (22MU.08 22MU.08 (22MU.08 (22MU.08 22MU.08 (22MU.08		08APR08 07MAY08 2
Design (AIP) submission for the SO's approval to the SO's approval from the SO's approval from the SO Cotain design (AIP) review by the SO Cotain design (AIP) approval from the SO Cotain design (AIP) approval for AIP Cotain design (AIP) Cotain design (AIP) approval for AIP Cotain design (AIP) approval for DIPA submission for the SO Cotain design (AIP) approval for DIPA at authorities approval for DIPA at authorities approval for DIPA Cotain design (AIP) approval for DIPA Cotain design (AIP) approval for AIP Cotain design (AIP) review by the rel authorities approval for AIP Cotain design (AIP) review by the rel authorities approval for AIP Cotain design (AIP) review by the rel authorities approval for AIP Cotain design (AIP) review by the rel authorities approval for AIP Cotain design (AIP) review by the rel authorities approval for AIP Cotain design (AIP) review by the SO Cotain design		08MAY08 22MAY08 2 285
Design (AIP) review by the SO CORRIGION CORRIGI		23MAY08 23MAY08 1
Application design (AIP) approval from the SO 0 22JULOB 2 2JULOB 2 2SB AIP submission for rel, authorities approval 1 23JULOB 22JULOB 1 229 Design (AIP) review by the rel, authorities approval for the DDA submission for the SOS approval 30 18JULOB 1/64/1068 2 286 Design (DDA) certification by the Design Checker 1 0.02EFDG 31/0CTDG 2 286 Design (DDA) certification by the Design Checker 1 0.02EFDG 1.02EFDG 1.229 Design (DDA) review by the SO 0 0.02EFDG 1.00FCDG 2.236 Design (DDA) review by the rel. authorities approval for DDA 1 0.0DECG 2.240 Design (DDA) review by the rel. authorities approval 1 0.0DECG 2.240 2.240 Design (DDA) review by the rel. authorities approval for DDA 1 0.0DECG 2.240 2.241 Design (AIP) review by the rel. authorities approval 1 0.0DECG 2.241 2.241 Design (AIP) review by the Des		24MAY08 22JUL08 2 285
After submission for rel. authorities approval 1 23JULOB 23JULOB 1 229 Design (Alf) review by the rel. authorities 15 24JULOB 07AUGOB 2 285 Obtain rel. authorities a paroval for Alborities 1 08AUGOB 2 285 Obtain SO's consent for design (AlP) 1 08AUGOB 2 285 Design (DbA) certification by the Design Checker 15 17AUGOB 31AUGOB 2 285 Design (DbA) certification by the Design Checker 15 17AUGOB 31AUGOB 2 285 Design (DbA) review by the SO 0 0 22SEPOB 31ACTOB 2 286 Design (DDA) review by the SO 0 0 22SEPOB 31ACTOB 2 286 Obtain design (DDA) review by the SO 0 0 22SEPOB 1 231 Design (DDA) review by the So 0 0 0 22BOVOB 2 241 Obtain sols consent for design (DDA) review by the Design Checker 15 0 0 2 241	T i	22JUL08 2 ·
Design (AIP) review by the rel. authorities 15 24JUL08 07AUG60 2 285		23JUL08 23JUL08 1
Obtain rel. author/ties's approval for AIP 1 08AUG08 08AUG08 1 228 Obtain SO's consent for design (AIP) 0 0 0AAUG08 2 285 Design preparation for the DDA submission changed by the Design Checker 15 17AUG08 1 229 Design (DDA) submission for the SO's approval 6 0.2SEP08 31OCT08 2 286 Design (DDA) review by the SO 0 31OCT08 2 286 Obtain design (DDA) review by the rest, authorities 28 02NOV08 2 286 Obtain design (DDA) review by the ret, authorities 28 02NOV08 2 286 Obtain and SO's consent for design (DDA) 0 30NU08 2 286 Obtain and SO's consent for the AIP submission for the SO's approval 1 07UN08 2 414 Design (AIP) review by the rel. SO's approval 1 22JUL08 2 414 Design (AIP) review by the SO 6 23JUL08 2 414 Design (AIP) review by the SO 6 23JUL08 2 414<	i	24JUL08 07AUG08 2 285
Obtain SO's consent for design (AIP) 0 09AUG08 2 285 Design preparation for the DDA submission 30 18.UL08 1 285 Design (DDA) certification by the Design Checker 15 17AUG08 1 229 Design (DDA) submission for the SO's approval 1 01SEP08 11229 286 Design (DDA) submission for the SO's approval from the SO 0 02SEP08 31OCT08 2 286 DDA submission for rel. authorities approval from the SO 0 02DC08 2 286 DDA submission for rel. authorities approval from Ed. authorities approval from DDA 0 0 02DC08 2 286 Obtain rel. authorities's approval from Ed. authorities approval from Ed. authorities approval from Ed. authorities 2 414 8 Design (AIP) review by the SO approval from the SO's approval 1 22JUL08 2.5SEP08 1 414 8 Design (AIP) review by the rel. authorities approval from the SO's approval 1 22SEP08 2.5SEP08 1 4 4 </th <th></th> <th>08AUG08 08AUG08 1</th>		08AUG08 08AUG08 1
Design (DDA) certification by the DDA submission 30 18JUL08 16AUG08 2 285 Design (DDA) certification by the Design Checker 15 17AUG08 1 228 Design (DDA) submission for the SO's approval 1 01SEP08 01SEP08 1 228 Design (DDA) submission for the SO's approval 6 02SEP08 31OCT08 2 286 Obania Mesign (DDA) approval from the SO 0 0 22NOV08 2 286 DDA submission for rel. authorities' approval from the SO 1 01NOV08 1 231 DDA submission for rel. authorities's approval from DDA 0 02DEC08 2 286 Obtain RO's consent for design (DDA) 0 0 02DEC08 2 414 Design for MA and MA/MT Connection 3 0 7.JUL08 2 414 Design for MA and MA/MT Connection 1 2.2UL08 2 414 8 Design (AIP) review by the SO's approval 1 2.2UL08 2 414 8 Design (AIP) review by the rel. author		09AUG08 2
Design (DDA) certification by the Design Checker 15 17AUG08 31AUG08 2 285 Design (DDA) submission for the SO's approval 1 01SEP08 01SEP08 1 229 Design (DDA) review by the SO 0 31OCT08 2 286 Obtain design (DDA) approval from the SO 0 31OCT08 2 286 DDA submission for rel. authorities approval from the SO 1 01NOV08 29NOV08 2 286 Obtain rel. authorities approval from the SO 1 01DEC08 1 221 231 Obtain SO's consent for design (DDA) 0 30 07JINNB 2 414 83 Design preparation for the AIP submission of the SO's approval 1 22JIL08 21JIL08 2 414 83 Design (AIP) review by the SO 0 23JIL08 2 414 41	" i	18JUL08 16AUG08 2 285
Design (DDA) submission for the SO's approval 1 01SEP08 1 229 Design (DDA) review by the SO 60 02SEP08 31OCT08 2 286 Obtain design (DDA) approval from the SO 0 31OCT08 2 286 DDA submission for rel. authorities' approval for DDA 1 01NOV08 07NOV08 2 286 Obtain rel. authorities's approval for DDA 1 01DEC08 1 231 Obtain SO's consent for design (DDA) 0 0 0 2 286 Design for MA and MAIMT Connection 0 <th></th> <th>17AUG08 31AUG08 2 285</th>		17AUG08 31AUG08 2 285
Design (DDA) review by the SO 60 Q2SEP08 31OCT08 2 286 Obtain design (DDA) approval from the SO 0 31OCT08 2 286 DDA submission for rel. authorities' approval 1 01NOV08 1 231 Design (DDA) review by the rel. authorities' approval for DDA 1 01DEC08 1 231 Obtain SO's consent for design (DDA) 0 02DEC08 2 286 Obtain SO's consent for design (DDA) 0 0 02DEC08 2 286 Design preparation for the AIP submission 30 07JUN08 2 414 8 Design (AIP) certification by the Design Checker 1 22JUL08 22JUL08 2 414 Design (AIP) review by the SO 60 23JUL08 20SEP08 2 414 AIP submission for rel. authorities 30 72SEP08 2 414 AIP submission for rel. authorities 4 1 22SEP08 2 414 AIP submission for rel. authorities' approval for AIP 1 22SEP08 2		01SEP08 01SEP08 1
Obtain design (DDA) approval from the SO 0 31OCT08 2 286 DDA submission for rel. authorities' approval 1 01NOV08 01NOV08 1 231 Design (DDA) review by the rel. authorities 28 02NOV08 29NOV08 2 286 Obtain rel. authorities's approval for DDA 1 01DEC08 1 231 Obtain SO's consent for design (DDA) 0 0 2DEC08 2 286 Obtain SO's consent for design (DDA) 0 0 0 20EC08 2 286 Design for MA and MAINT Connection 30 07JUL08 2 414 8 Design for MA and MAINT Connection 30 07JUL08 2 414 8 Design for MA and MAINT Connection 1 22JUL08 2 414 8 Design (AIP) certification by the Design Checker 1 22JUL08 2 414 AIP submission for rel. authorities' approval for AIP 1 22JUL08 2 414 AIP submission for rel. authorities' approval for AIP 0		02SEP08 31OCT08 2
DDA submission for rel. authorities' approval 1 01NOV08 01NOV08 1 231 Design (DDA) review by the rel. authorities 28 02NOV08 29NOV08 2 286 Obtain rel. authorities's approval for DDA 1 01DEC08 01DEC08 1 234 Design for MA and MA/MT Connection 30 07JUN08 06JUL08 2 414 Design preparation for the AIP submission 15 07JUL08 21JUL08 2 414 Design (AIP) certification by the Design Checker 15 07JUL08 21JUL08 2 414 Design (AIP) submission for the SO's approval 1 22JUL08 2414 444 Design (AIP) review by the SO 60 23JUL08 2414 444 AIP submission for rel. authorities' approval for AIP 1 22SEP08 23SEP08 1 AIP submission for the DDA submission 0 23JUL08 2 413 Design preparation for the DDA submission for the SO's approval 1 03DOV08 1 413 Design (DDA) submission for the SO's approval </th <th> </th> <th>31OCT08 2</th>		31OCT08 2
Design (DDA) review by the rel. authorities 28 02NOV08 29NOV06 2 286 Obtain rel. authorities's approval for DDA 1 01DEC08 01DEC08 1 231 Obtain SO's consent for design (DDA) 0 20DEC08 2 286 Design for MA and MAIMT Connection 30 07JUL08 2 1JUL08 2 414 Design for MA and MAIMT Connection 15 07JUL08 21JUL08 2 414 Design (AIP) certification by the Design Checker 15 07JUL08 2JUL08 2 414 Design (AIP) submission for the SO's approval 1 2ZJUL08 2SJUL08 2 414 Obtain design (AIP) approval from the SO 0 23JUL08 2SJEP08 1 335 AIP submission for rel. authorities's approval for AIP 1 2SSEP08 2 414 Obtain SO's consent for design (AIP) 0 0 0 0 0 413 Design preparation for the DDA submission 15 17OCT08 2 413 Design (DDA) sertification by the SO	1	01NOV08 01NOV08 1
Obtain rel. authorities's approval for DDA 1 01DECO8 1 231 Design (AIP) review by the Design (AIP) review by the Design (AIP) consent for design (AIP) continuities's approval for the SO's approval 1 22JUL08 22JUL08 2 414 Image: Consent for the AIP submission for the SO's approval 1 22JUL08 22JUL08 2 414 Image: Consent for the SO's approval 1 22JUL08 2DIL08 2 414 Image: Consent for the SO's approval for SO's Consent for the SO's approval for SO's approval for SO's approval for SO's approval for SO's Consent for SO's AIDECON for SO's Consent for SO		02NOV08 29NOV08 2
Design for MA and MA/MT Connection 30 07JUN0B 02DEC08 2 286 Design for MA and MA/MT Connection 30 07JUN0B 06JUL0B 2 414 Design preparation for the AIP submission 15 07JUL0B 2JUL0B 2 414 Design (AIP) certification by the Design Checker 15 07JUL0B 2JUL0B 2 414 Design (AIP) review by the SO 0 23JUL0B 2OSEP0B 2 414 AIP submission for rel. authorities 0 23JUL0B 2SSEP0B 1 335 Obtain design (AIP) review by the rel. authorities 1 2ZSEP0B 2 414 AIP submission for rel. authorities's approval for AIP 1 22SEP0B 22SEP0B 1 337 Obtain rel. authorities's approval for AIP 1 08OCT0B 09OCT0B 1 413 Obtain rel. authorities's approval for AIP 0 0 0 0 0 0 Obtain rel. authorities's approval for the DDA submission for the DDA submission for the SO's approval 1 0 0		01DEC08 01DEC08 1
Design for MA and MAMT Connection 30 07JUN08 65JUL08 2 414 ESS Design preparation for the AIP submission or the SO's approval 15 07JUL08 21JUL08 2 414 B Design (AIP) submission for the SO's approval 1 22JUL08 22JUL08 2 414 Design (AIP) review by the SO 0 23JUL08 2 414 AIP submission for rel. authorities 1 22SEP08 2 414 AIP submission for rel. authorities 15 23SEP08 22SEP08 1 335 Obtain rel. authorities's approval for AIP 1 08OCT08 2 413 Obtain rel. authorities's approval for AIP 0 0 20SEP08 1 337 Obtain rel. authorities's approval for AIP 1 08OCT08 2 413 Obtain rel. authorities's approval for AIP 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 <th></th> <th>02DEC08 2</th>		02DEC08 2
Design preparation for the AIP submission 30 07JUN08 66JUL08 2 414 Design (AIP) certification by the Design Checker 15 07JUL08 21JUL08 2 414 Design (AIP) submission for the SO's approval 1 22JUL08 22JUL08 2 414 Design (AIP) review by the SO 0 20SEP08 2 414 AIP submission for rel. authorities' approval 1 22SEP08 2 413 Design (AIP) review by the rel. authorities 15 23SEP08 2 413 Obtain SO's consent for design (AIP) 0 0 0 0 0 Obtain SO's consent for design (AIP) 0 0 0 0 0 0 Obtain SO's consent for design (AIP) 0 0 0 0 0 0 0 Design (DDA) certification by the Design Checker 15 17COT08 2 413 Design (DDA) review by the SO 0 0 0 0 0 0 Design (DDA) review by the SO 0	Permanent Design for MA and MA/MT Connection	
Design (AIP) certification by the Design Checker 15 07JUL08 21JUL08 2 414 Design (AIP) submission for the SOs approval 1 22JUL08 22JUL08 2 414 Design (AIP) review by the SO 0 23JUL08 2 414 Obtain design (AIP) approval from the SO 0 20SEP08 2 414 AIP submission for rel. authorities' approval 1 22SEP08 2 413 Design (AIP) review by the rel. authorities 15 23SEP08 2 413 Obtain rel. authorities's approval for AIP 1 08OCT08 2 413 Obtain SO's consent for design (AIP) 0 0 09OCT08 2 413 Design preparation for the DDA submission 30 17SEP08 16OCT08 2 413 Design (DDA) certification by the Design Checker 15 17OCT08 2 413 Design (DDA) review by the SO 60 0 2NOV08 2 141	- 1	07JUN08 06JUL08 2 414
Design (AIP) submission for the SO's approval 1 22JUL08 22JUL08 1 338 Design (AIP) review by the SO 60 23JUL08 20SEP08 2 414 Obtain design (AIP) approval from the SO 0 22SEP08 2 414 AIP submission for rel. authorities' approval from the SO 1 22SEP08 1 335 Design (AIP) review by the rel. authorities 15 23SEP08 07OCT08 413 Obtain rel. authorities's approval for AIP 1 08OCT08 07OCT08 413 Obtain rel. authorities's approval for AIP 0 09OCT08 413 Obtain CO's consent for design (AIP) 0 413 Design (DDA) certification by the Design Checker 15 17OCT08 2 413 Design (DDA) review by the SO 60 02NOV08 01NOV08 1 414	- 1	07JUL08 21JUL08 2 : 414
Design (AIP) review by the SO 60 23JUL08 20SEP08 2414 Obtain design (AIP) approval from the SO 0 20SEP08 2414 AIP submission for rel. authorities' approval 1 22SEP08 1 335 Design (AIP) review by the rel. authorities 15 23SEP08 07OCT08 2 413 Obtain rel. authorities's approval for AIP 1 08OCT08 07OCT08 2 413 Obtain SO's consent for design (AIP) 0 0 09OCT08 2 413 Design (DDA) certification by the Design Checker 15 17OCT08 31OCT08 2 413 Design (DDA) submission for the SO's approval 1 01NOV08 01NOV08 1 337 Design (DDA) review by the SO 60 02NOV08 31DEC08 2 414	1	22JUL08 22JUL08 1
Obtain design (AIP) approval from the SO 0 20SEP08 2 414 AIP submission for rel. authorities 1 22SEP08 1 335 Design (AIP) review by the rel. authorities's approval for AIP 1 08OCT08 2 413 Obtain rel. authorities's approval for AIP 0 0 00CT08 2 413 Obtain rel. authorities's approval for AIP 0 0 0 413 Design CAIP submission for the DAS submission for the SO's approval 1 0 0 0 413 Design (DDA) review by the SO 40 1 0 0 0 413		23JUL08 20SEP08 2 414
AIP submission for rel. authorities' approval 1 22SEP08 22SEP08 1 335 Design (AIP) review by the rel. authorities 15 23SEP08 07OCT08 2 413 Obtain rel. authorities's approval for AIP 1 08OCT08 1 337 Obtain SO's consent for design (AIP) 0 0 413 Design preparation for the DDA submission 30 17SEP08 16OCT08 2 413 Design (DDA) certification by the Design Checker 15 17OCT08 31OCT08 2 413 Design (DDA) submission for the SO's approval 1 01NOV08 01NOV08 1 337 Design (DDA) review by the SO 60 02NOV08 31DEC08 2 414		20SEP08 2
Design (AIP) review by the rel. authorities 15 23SEP08 07OCT08 2 413 Obtain rel. authorities's approval for AIP 1 08OCT08 1 337 Obtain SO's consent for design (AIP) 0 0 09OCT08 2 413 Design preparation for the DDA submission 30 17SEP08 16OCT08 2 413 Design (DDA) certification by the Design Checker 15 17OCT08 31OCT08 2 413 Design (DDA) submission for the SO's approval 1 01NOV08 01NOV08 1 337 Design (DDA) review by the SO 60 02NOV08 31DEC08 2 414		22SEP08 22SEP08 1
Obtain rel. authorities's approval for AIP 1 08OCT08 1 337 Obtain SO's consent for design (AIP) 0 0 09OCT08 2 413 Design preparation for the DDA submission 30 17SEP08 16OCT08 2 413 Design (DDA) certification by the Design Checker 15 17OCT08 31OCT08 2 413 Design (DDA) submission for the SO's approval 1 01NOV08 01NOV08 1 337 Design (DDA) review by the SO 60 02NOV08 31DEC08 2 414		23SEP08 07OCT08 2
Obtain SO's consent for design (AIP) 0 09OCT08 2 413 Design preparation for the DDA submission 30 17SEP08 16OCT08 2 413 Design (DDA) certification by the Design Checker 15 17OCT08 31OCT08 2 413 Design (DDA) submission for the SO's approval 1 01NOV08 01NOV08 1 337 Design (DDA) review by the SO 60 02NOV08 31DEC08 2 414		08OCT08 08OCT08 1
Design preparation for the DDA submission 30 17SEP08 16OCT08 2 413 Design (DDA) certification by the Design Checker 15 17OCT08 31OCT08 2 413 Design (DDA) submission for the SO's approval 1 01NOV08 1 337 Design (DDA) review by the SO 60 02NOV08 2 414	- :	09OCT08 2
Design (DDA) certification by the Design Checker 15 17OCT08 31OCT08 2 Design (DDA) submission for the SO's approval 1 01NOV08 01NOV08 1 Design (DDA) raview by the SO 60 02NOV08 31DEC08 2		17SEP08 16OCT08 2 413
Design (DDA) review by the SO approval 101NOV08 01NOV08 1 Design (DDA) review by the SO 60 02NOV08 31DEC08 2		17OCT08 31OCT08 2
Design (DDA) review by the SO 60 02NOV08 31DEC08 2		01NOV08 01NOV08 1
	_	02NOV08 31DEC08 2

Į.

	Shoot 20 of 42	
	28 11MAR09 07APR09 2 323	02L1GG0132 Design (DDA) review by the rel. authorities
	10MAR09 10MA	
•	R09 2	
	60 09JAN09 09MAR09 2 323	
	h	02L1GG0124 Design (DDA) submission for the SO's approval
413	7	02L1GG0122 Design (DDA) certification by the Design Checker
	0	02L1GG0120 Design preparation for the DDA submission
	16DEC08 2	02L1GG0118 Obtain SO's consent for design (AIP)
	1 15DEC08 15DEC08 1 260	02L1GG0116 Obtain rel. authorities's approval for AIP
Fix	15 30NOV08 14DEC08 2 323	02L1GG0114 Design (AIP) review by the rel. authorities
	1 29NOV08 29NOV08 1 260	02L1GG0112 AIP submission for ref. authorities' approval
	0 28NOV08 2 322	02L1GG0110 Obtain design (AIP) approval from the SO
	60 30SEP08 28NOV08 2 322	02L1GG0108 Design (AIP) review by the SO
	1 29SEP08 29SEP08 1 260	02L1GG0106 Design (AIP) submission for the SO's approval
122	15 14SEP08 28SEP08 2 322	02L1GG0104 Design (AIP) certification by the Design Checker
	30 15AUG08 13SEP08 2 322	02L1GG0102 Design preparation for the AIP submission
		Drainage Impact Assessment
		Design Pawages to Works in Portion C
*	0 14AUG08 2 322	02L1CC0736 Obtain SO's consent for design (DDA)
	1 13AUG08 13AUG08 1 259	02L1CC0734 Obtain rel. authorities's approval for DDA
	28 16JUL08 12AUG08 2 321	02L1CC0732 Design (DDA) review by the rel. authorities
	1 15JUL08 15JUL08 1 259	02L1CC0730 DDA submission for rel. authorities' approval
•	0 14JUL08 2 321	02L1CC0728 Obtain design (DDA) approval from the SO
	28 17JUN08 14JUL08 2 321	02L1CC0726 Design (DDA) review by the SO
	1 16JUN08 16JUN08 1 259	02L1CC0724 Design (DDA) submission for the SO's approval
PEC .	15 31MAY08 14JUN08 2 319	02L1CC0722 Design (DDA) certification by the Design Checker
	30 01MAY08 30MAY08 2 319	02L1CC0720 Design preparation for the DDA submission
•	0 Z3MAY08 2 319	02L1CC0718 Obtain SO's consent for design (AIP)
	1 22MAY08 22MAY08 1 261	02L1CC0716 Obtain rel. authorities's approval for AIP
	28 24APR08 21MAY08 2 319	02L1CC0714 Design (AIP) review by the rel. authorities
	1 23APR08 23APR08 1 260	02L1CC0712 AIP submission for rel. authorities' approval
•	0 22APR08 2 318	02L1CC0710 Obtain design (AIP) approval from the SO
	28 26MAR08 22APR08 2 318	02L1CC0708 Design (AIP) review by the SO
	1 25MAR08 25MAR08 1 259	02L1CC0706 Design (AIP) submission for the SO's approval
623	15 09MAR08 23MAR08 2 319	02L1CC0704 Design (AIP) certification by the Design Checker
	15 23FEB08 08MAR08 2 262	02L1CC0702 Design preparation for the AIP submission
		Boulder Assessment & Design for Stabili. Measure
•	0 02FEB09 2 413	02L1CC0636 Obtain SO's consent for design (DDA)
	1 31JAN09 31JAN09 1 337	02L1CC0634 Obtain rel. authorities's approval for DDA
	28 03JAN09 30JAN09 2 413	02L1CC0632 Design (DDA) review by the rel. authorities
	1 02JAN09 02JAN09 1 334	02L1CC0630 DDA submission for rel. authoritles' approval
80.00 (2	208 2	02L1CC0628 Obtain design (DDA) approval from the SO
EMANASIA KROINDAIFMAMBITA BIONDO FINAMISIA BIONDO FAMAMISIA BODO PARAMINI A BIONDO FAMAMISI A BODO	Start Hrish D	
	A A	Activity

	Shoot 21 of 42	
	28 03DEC08 30DEC08 2 464	102L1FE0132 Design (DDA) review by the rel. authorities
		- 1
	0 01DEC08 2 464	. !
	30 02NOV08 01DEC08 2 464	02L1FE0126 Design (DDA) review by the SO
	- -	02L1FE0124 Design (DDA) submission for the SO's approval
	170CT08 310CT08 2	1
	17SEP08 16OCT08 2	02L1FE0120 Design preparation for the DDA submission
•	708 2	02L1FE0118 Obtain SO's consent for design (AIP)
	30SFP08 30SFP08 1	
	OSSEDOR SOSSEDOR	02L1FE0114 Design (AIP) review by the rel authorities
	01SEP08 01SEP08 1	_
	 	02L1FE0110 Obtain design (AIP) approval from the SO
	30 01AUG08 30AUG08 2 466	02L1FE0108 Design (AIP) review by the SO
	1 31JUL08 31JUL08 1 379	02L1FE0106 Design (AIP) submission for the SO's approval
22	15 16JUL08 30JUL08 2 466	02L1FE0104 Design (AIP) certification by the Design Checker
2.5	15 01JUL08 15JUL08 2 466	02L1FE0102 Design preparation for the AIP submission
		Design for Communication System
		Design Replace for Extit Works
•	0 07FEB09 2 631	02L1GG0328 Obtain design (DDA) approval from the SO
	28 11JAN09 07FEB09 2 631	02L1GG0326 Design (DDA) review by the SO
	1 10JAN09 10JAN09 1 510	021.1GG0324 Design (DDA) submission for the SO's approval
	26DEC08 09JAN09 2	02L1GG0322 Design (DDA) certification by the Design Checker
	2	02L1GG0320 Design preparation for the DDA submission
	11DEC08 2	02L1GG0310 Obtain design (AIP) approval from the SO
	14NOV08 11DEC08 2	02L1GG0308 Design (AIP) review by the SO
	1 13NOV08 13NOV08 1 509	02L1GG0306 Design (AIP) submission for the SO's approval
	2	02L1GG0304 Design (AIP) certification by the Design Checker
	15 14OCT08 28OCT08 . 2 630	02L1GG0302 Design preparation for the AIP submission
		ELS Design for Pipe Jacking at Portion G
•	0 24JAN09 2 438	02L1GG0228 Obtain design (DDA) approval from the SO
	28 28DEC08 24JAN09 2 438	02L1GG0226 Design (DDA) review by the SO
	1 27DEC08 27DEC08 1 354	02L 1GG0224 Design (DDA) submission for the SO's approval
	15 11DEC08 25DEC08 2 439	02L1GG0222 Design (DDA) certification by the Design Checker
	2	02L1GG0220 Design preparation for the DDA submission
	2	02L1GG0210 Obtain design (AIP) approval from the SO
	2	02L1GG0208 Design (AIP) review by the SO
	-	02L1GG0206 Design (AIP) submission for the SO's approval
		02L1GG0204 Design (AIP) certification by the Design Checker
	30 14SEP08 13OCT08 2 439	02L1GG0202 Design preparation for the AIP submission
		Temp. Platform Design for H-Piling at Portion G
	0 09APR09 2 323	02L1GG0136 Obtain SO's consent for design (DDA)
250 100 100 100 100 100 100 100 100 100 1	08APH09 1	02L1GG0134 Obtain rel. authorities's approval for DDA
MANNOTANSONDES SOND SERVICE OF THE SOND SERVICE OF THE SOND SERVICE OF THE SOND SERVICE OF THE S	Set Set Pior	Description
2008 Company of the Control of the C	Early	TIB THE THE PARTY OF THE PARTY

		1,286	18MAR09 2		0	02L10D1046 2L 23; On completion of all works under this CC
		1,325	07FEB09 2		0	·
	•	1,383	11DEC08 2		0	
	•	1,469	16SEP08 2		0	
	•	1,529	18JUL08 2		0	- 1
	•	1,584			0	
	•	1,644	25MAR08 2		0	1
,		1,286	18MAR09 2		0	
	-	1,415	09NOV08 2		0	
		11,363	31DEC08 2		0	
	•	1,423	01NOV08 2		0	
	•	1,465	20SEP08 2		0	\neg
	•	1,525	22JUL08 2		0	- 1
		1,351	12JAN09 2		0	1
			13NOV08 2		0	
	•	:	03OCT08 2		0	02L10D1016 2L 8; On acceptance of AIP by the SO; Portion B
	•	į.	04AUG08 2		0	02L10D1014 2L 7; On submission of AIP to the SO; Portion B
	•	Ė	14OCT08 2		0	ĺ
	•	F			0	02L10D1010 2L 5; On subumission of DDA to the SO; Portion A
	•				0	02L10D1008 2L 4; On acceptance of AIP by the SO; Portion A
	•	1	808		0	02L10D1006 2L 3; On submission of AIP to the SO; Portion A
	•	1	H08		0	02L10D1004 2L 2; On acception of PDP by the SO
	• • • •	1 719	10.JAN08 2		0	02L10D1002 2L 1; On submission of PDP to the SO
						Sonediie o Milestotes Ton 6051: Centra No. 21:
	•	818	29OCT08 2		0	102L1FE0228 Obtain design (DDA) approval from the SO
	區	818	29OCT08 2	30SEP08	8	
		664	29SEP08 1	29SEP08	-	02L1FE0224 Design (DDA) submission for the SO's approval
	NW.	ļ	80,	14SEP08	15	
			ļ	15AUG08	30	i
	•	-	30AUG08 2		0	02L1FE0210 Obtain design (AIP) approval from the SO
	Œ	+ -	308	01AUG08	90	
			80	317008	-	02L1FE0206 Design (AIP) submission for the SO's approval
	12%	1.	ļ.	16JUL08	15	
	EX	818	15JUL08 2	01JUL08	15	02L1FE0202 Design preparation for the AIP submission
						Design for Flow Measurement System
		2 464	601		0	02L1FE0136 Obtain SO's consent for design (DDA)
12 KW KK K K K K K K K K K K K K K K K K	A TO CHE TO THE	Ē	C08	31DEC08	1	02L1FE0134 Obtain rel. authorities's approval for DDA
DIE MAMIETASIONIO DE MAJULIA SIONIO DIFIMAMUNTA SIONIO PERA	DISFMANUTUAISCIN		Early C	Early Sart	B.O	Activity Description
THE SECRETARY CONTRACTOR CONTRACT	The Party of The Party of the Constitution of the Party o	Ż	では、おいま	15		

ĺ

4
₽
24
leet
ঠ

45 ZAAPR09 (10,11/10) 2 0 0 CH4460-426/m=Corcurrent with TBM advances; V 2 ZAAPR09 (10,11/10) 2 0 0 133,11/100 (12,11/10) 2 0 0 CH4460-426/m=Corcurrent with TBM advances; V 2 131,11/100 (12,11/10) 2 0 0 CH500 (10,11/10) 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	アンドでは、他のでは、これには、これには、これには、これには、これには、これには、これには、これに			
Wide control of particular and the particular of the particular	Verify method stateme	굒	26APR09 2	0
Subsequent (Fight Control attain goals) 2 11,11/10/10 2,11/10/			10JUN09	
WED Trans states operation 0 32,01/200 20,000/2006 1000	- 1	} 	12JUN09	
Control growing between the strategy of predictions and the	3AL1FT0624 WSD Tunnel starts operation	<u> </u>	JN09 2	•
Carry out gouling trials from the surface at F 30 28AMYY06 30LUN08 1 100 100	MBN ASSERTION CATHURATION OF SERVING WORK			
Title Heider asseminy 3 servicy test 22 (10,0700) 10,050000 10,050000 10,050000 10,0500	3AL1FT0700 Carry out drouging from the surface at E1	-	4	170 COC CLIENT
TBM mobilisation to turned fixed CHRitish TBM mobilisation to turned fixed CHRITISH TBM advances: CHRISOS-5035 11 220EC08 10 CHRISOS 10	TBM initial assembly & start-up test	+	008	(countries of DOC) in the months of DOC the design of pre-excavation grouning at
This black-up space to Classification Conveyed colors Classification Classification	Ţ~``;	-		
This advances (1960-54075 1960-10-10-10-10-10-10-10-10-10-10-10-10-10		†		
TRM advances; PT CREGOTS-GOOD 11 2000 17				
Halls buck-up system (6 decks) 10 GrANN9 17JAN9 14 CANN9 17JAN9 14 CANN9 14 CANN			·	
TRM advances; PC CHSD03-SOD5 TRM advances; CHSD04-SEG5 TRM advances; CHSD04-SEG5	1			
Install black-up system; (1 decks)				#Fault P7; CH5033
TBM advances; CH 5005-5000		∤ 	┧	
Tibil advances; WSDYKVTW/Tibic CH5000-4655 9 0 07FEBG9 1 0 0 0 CH500004953WSD Yau Kom Waler Trealment Works & Pault Féc COrrespondences; WSD VKVTW/TW/Fib C CH4664-4550 0 1 17FEBG9 2 1 0 0 17FEBG9 2 1 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	7		ļ	
Conneyor bell sys	Ť		 	
Pack Deceased paper vision Pack Deceased Pack Deceased Deceased	- 1		 	
Page Deceases Page Pag	3AL1FT0722 Install noise enclosure	i	ļ -	
Papply to EPD for CNP for 24 hrs. turnel work	Walk Hurnel Works Day, Calign Wolf			
FPD process/approve CNP application 45 06NOV08 20DECOR 2 77 TBM advances; CH4530-4350 3 24AFR09 10 10 10 10 10 10 10 TBM advances; CH4530-4320 3 24AFR09 10 10 10 10 10 10 TBM advances; CH4530-4320 3 24AFR09 10 10 10 10 10 10 TBM advances; CH4530-4320 3 24AFR09 10 10 10 10 10 10 TBM advances; CH4530-4320 3 24AFR09 10 10 10 10 10 10 TBM advances; CH4530-4320 3 24AFR09 10 10 10 10 10 TBM advances; CH4530-4320 3 24AFR09 10 10 10 10 10 TBM advances; CH4530-4320 3 24AFR09 10 10 10 10 10 TBM advances; CH4530-4320 4 11 10 10 10 10 10 TBM advances; CH4530-4320 4 11 10 10 10 10 10 TBM advances; CH4530-4320 4 11 10 10 10 10 10 TBM advances; CH4530-4320 4 11 10 10 10 10 10 TBM advances; CH4530-4320 4 11 10 10 10 10 10 10		}-	2	[Q0
TBM advances: WSD YKTVITW/F8c CH4963-4830 16 o7MAR09 28MAR09 1 o o o o o o o o o o o o o o o o o o	1 "	Ť	5	
TBM advances; CH4830-4760 3 26NAR09 28NAR09 1 0 24NAR09 1 0 1 1 1 1 2 </td <td>1</td> <td>ţ</td> <td>- - -</td> <td>More-excavation orduting (@20m/1.5dayexdavation/pea-gravel/Inion @2</td>	1	ţ	- - -	More-excavation orduting (@20m/1.5dayexdavation/pea-gravel/Inion @2
TBM advances; FBb CH4760-4740 3 30MARR99 16APR99 1 0 0 1	ļ .	† ·		(@ 21m/day
TBM advances; CH4740-4555 9 02APR09 16APR09 1 0 17APR09 1 0 17AP	;	1	NR09 01APR09 1	tion grouting @ 20m/1
TBM advances; P6a CH4555-4510 6 17APR09 23APR09 1 0 0 0 TBM advances; CH4510-4460 36 27APR09 10JUN09 1 0 0 TBM advances; P6 CH4260-4250 4 11JUN09 15JUN09 1 0 0 TBM advances; P6 CH4260-4220 4 11JUN09 15JUN09 1 0 0 TBM advances; P6 CH4260-4220 3 08JUL09 1 0 0 TBM advances; P6 CH4260-4220 3 08JUL09 1 0 0 TBM advances; P6 CH4260-4220 3 08JUL09 1 0 0 TBM advances; P6 CH320-3875 12 11JUL09 1 0 0 TBM advances; P6 CH320-3575 13 13AUG09 1 0 0 TBM advances; P3 CH3143-3125 2 04SEP09 1 8 TBM advances; P3 CH3143-3125 2 04SEP09 1 8 TBM advances; CH3125-2970 7 07SEP09 1 8 TBM advances; CH3125-2450 7 04SEP09 1 8 TBM advances; CH3125-450 7 04SEP09 1 8 TBM advan	1	· · · · ·	'R09 16APR09 1	₩@ 21m/day
TBM advances; CH4510-4460 36 27APR09 10,UlN09 1 0 1 1 1 1 1 1 1 1	;	†	'R09 23APR09 1	
TBM advances; WSD T3/P6 CH4460-4250 36 27APR09 10JUN09 1		-	. ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ ـ	
TBM advances; P6 CH4250-4220 4 11JUN09 15JUN09 1 IF TBM advances; CH4220-3840 18 16JUN09 07JUL09 1 8 TBM advances; CH3820-3875 12 11JUL09 24JUL09 1 8 TBM advances; P4 CH3575-3525 6 25JUL09 1 8 1 TBM advances; P4 CH3575-3525 6 25JUL09 1 8 1 TBM advances; P4 CH3575-3526 6 25JUL09 1 8 1 TBM advances; P4 CH3575-3526 6 25JUL09 1 8 1 TBM advances; P4 CH3575-3308 10 13AUG09 27AUG09 1 8 TBM advances; P3 Noise sestitive area CH3308-3175 13 13AUG09 27AUG09 1 8 TBM advances; P3 CH3143-3125 2 04SEP09 1 8 Pre-excavation grouting @ 2dm/1.5 TBM advances; CH3125-2970 7 07SEP09 1 8 Pre-excavation grouting @ 2dm/1.5 TBM advances; WSD WS Reservior CH2970-2865 13 15SEP0				
TBM advances; OH320-3840 18 16JUN09 07JUL09 1 6 TBM advances; P5 CH3840-3820 3 08JUL09 1 8 7 11JUL09 1 8 7 1.5da				Fault P6 OH4250-4220pre-excavation grouting @ 20m/1
TBM advances; P5 CH3840-3820 3 08JUL09 10JUL09 1 8 Pre-excavation grouting @ 20m/1.5da TBM advances; CH3820-3575 12 11JUL09 24JUL09 1 8 Pre-excavation grouting @ 20m/1.5da TBM advances; CH3525-3308 10 01AUG09 12AUG09 1 8 Pre-excavation grouting @ 20m/1.5da TBM advances; CH3525-3308 10 01AUG09 12AUG09 1 8 Pre-excavation grouting @ 20m/1.5da TBM advances; P3/Noise sesitive area CH3175-3143 6 28AUG09 03SEP09 1 8 Pre-excavation grouting @ 20m/1.5c TBM advances; P3 CH3143-3125 2 04SEP09 1 8 Pre-excavation grouting @ 20m/1.5c TBM advances; CH3125-2970 7 07SEP09 1 8 Pre-excavation grouting @ 20m/1.5c TBM advances; WSD WS Reservior CH2970-2865 13 15SEP09 1 8 Pre-excavation grouting @ 20m/1.5c			N09: 07JUL09 1	
TBM advances; CH3820-3575 12 11JUL09 24JUL09 1 8 re-excavation grouting @ 20m/1.5da TBM advances; CH3575-3525 6 25JUL09 31JUL09 1 8 re-excavation grouting @ 20m/1.5da TBM advances; CH3525-3308 10 01AUG09 12AUG09 1 8 re-excavation grouting @ 20m/1.5da TBM advances; P3/Noise sesitive area CH3175-3143 6 28AUG09 03SEP09 1 8 re-excavation grouting @ 20m/1.5c TBM advances; P3 CH3143-3125 2 04SEP09 14SEP09 1 8 pre-excavation grouting @ 20m/1.5c TBM advances; CH3125-2970 7 07SEP09 1 8 pre-excavation grouting @ 20m/1.5c				
TBM advances; P4 CH3575-3525 6 25JUL09 31JUL09 1 8 (PP-excáva de excáva exemitive area CH3308-3175 10 01AUG09 12AUG09 1 8 PP-excáva de excáva de excáva de excéptive area CH3308-3175 13 13AUG09 27AUG09 1 8 PP-excáva de excéptive area CH3175-3143 6 28AUG09 03SEP09 1 8 PP-excéptive area CH3175-3143 7 07SEP09 1 8 PP-excéptive area CH3175-2970 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 3 2 3 2 3 3 3 3 3 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4				
TBM advances; CH3525-3308 10 01AUG09 12AUG09 1 8 TBM advances; Noise sestitive area CH308-3175 13 13AUG09 27AUG09 1 8 TBM advances; P3/Noise sestitive area CH3175-3143 6 28AUG09 03SEP09 1 8 TBM advances; P3 CH3143-3125 2 04SEP09 05SEP09 1 8 TBM advances; CH3125-2970 7 07SEP09 1 8 pre-exca TBM advances; WSD WS Reservior CH2970-2865 13 15SEP09 1 8 pre-exca				ė.
TBM advances; Noise sestitive area CH3175-3143 6 28AUG09 27AUG09 1 8 7 TBM advances; P3 CH3143-3125 2 04SEP09 05SEP09 1 8 pre-exca TBM advances; P3 CH3143-3125 2 04SEP09 05SEP09 1 8 pre-exca TBM advances; CH3125-2970 7 07SEP09 14SEP09 1 8 pre-exca TBM advances; WSD WS Reservior CH2970-2865 13 15SEP09 29SEP09 1 8 pre-exca				
TBM advances; P3/Noise sesifive area CH3175-3143 6 28AUG09 03SEP09 1 8 pre-exca TBM advances; P3 CH3143-3125 2 04SEP09 05SEP09 1 8 pre-exca TBM advances; CH3125-2970 7 07SEP09 14SEP09 1 8 TBM advances; WSD WS Reservior CH2970-2865 13 15SEP09 29SEP09 1 8				
TBM advances; CH3125-2970 7 07SEP09 1 8 pre-ex TBM advances; CH3125-2970 7 07SEP09 14SEP09 1 8 TBM advances; WSD WS Reservior CH2970-2865 13 15SEP09 29SEP09 1 8 pre-ex		-	L	
TBM advances; CH3125-2970 7 07SEP09 14SEP09 1 8 Pere- TBM advances; WSD WS Reservior CH2970-2865 13 15SEP09 295EP09 1 8 pre-e			P09 05SEP09 : 1	pre-exca
TBM advances; WSD WS Reservior CH2970-2865 13 15SEP09 29SEP09 1 8			P09 14SEP09 1	
	3AL1FT0840 TBM advances; WSD WS Reservior CH2970-2865	i	P09 : 29SEP09 1	pre-excavation arduting @ 2bm/1.5dav8

	1 10 to to				
	709 2 14,080	100CT	0	oan 13, On completion of grouting wks at F5	
CH 2865-2970 Tsugn Wan West Service Reservior Group	2	29SEP09	0	6aR 14; On completion of grouting wks at WSD's	6AR1FT0928
	1 0	05SEP09	0	6aR 13; On completion of grouting wks at P3	6AR1FT0926
	6	31.11.1	0	6aR 12; On completion of grouting wks at P4	6AR1FT0924
	v 01	10JUL09	0	6aR 11; On completion of grouting wks at P5	6AR1FT0922
	1 0	15.II INDO	0	6aR 10; On completion of grouting works at P6	6AR1FT0920
•	1 0	60NI N'SO	0	6aR 9; On completion of 80% grout by Ith at P6	6AR1FT0918
	1 0	26MAY09	C	6aR 8; On completion of 60% grout by Ith at P6	6AR1FT0916
> 4	1 0	16MAY09	0	6aR 7; On completion of 40% grout by Ith at P6	6AR1FT0914
	1 0	07MAY09	0	6aR 6; On completion of 20% grout by Ith at P6	6AR1FT0912
•	٦	10,1	0	6aR 5; On completion of grouting at WSD T. 3	6AR1FT0910
	71	23AF	0	6аЯ 4; On completion of grouting at F6a	6AR1FT0908
	2	01AF	0	6aR 3; On completion of grouting at F6b	6AR1FT0906
	1	25M/	0	6aR 2; On completion of grouting at F6c	6AR1FT0904
	AN09 2 1,334	29JAN	0	6aR 1; On completion of grouting at P7	6AR1FT0902
	EB11 2 577	05FEB11 25FE	24	SO issues completion certificate	3AL1FT0888
		i -	0	Handover of Portion F	3AL1FT0886
	811 2 5	·‡	7	Contractor serve notice for Works completion	3AL1FT0884
	-	04DEC10 28J/	45	Authorities' inspection/remedial works; daytime	3AL1FT0882
Exercised 2		- †	28	Testing & Commissioning; daytime	3AL1FT0880
	V10 1	-+	06	Installation of communication system (Daytime)	3AL1FT0878
rpoor comprehensive comprehensive comprehensive comprehensive to the comprehensive co	-	·÷	99	Complete maintennce access & dry weather channel	3AL1FT0876
100 m	Y10 1 1	22DEC08	414	Back grouting (daytime); CH5100-00	3AL1FT0874
Extract of the Court of the Cou	-		50*	Desembly & demobilization of TBM	3AL1FT0873
Dre-excavation arounds to the provider	V10 1	27MAR10 14M	37	TBM advances; F1 CH300-0	3AL1FT0872
	/R10 1	15MAR10 26MA	=	TBM advances; CH530-300	3AL1FT0870
CIO Z IM/OBJ	NB10 1	13MAR10 13MA	+	TBM advances; P1 CH540-530	3AL1FT0868
	R10 . 1	. .	11	TBM advances; CH770-540	3AL1FT0866
nre-excevation mainting @ 20m/1 EHm.4		+		TBM advances; P2 CH795-770	3AL1FT0864
Manager Arthur Britain & Control of Control	810 1	·	2	7	3AL1FT0862
pre-exception arouting a 20m / 15 1 m/day	N10 - 1	-	3	TBM advances; F2 CH1250-1230	3AL1FT0860
pow advance rate 10.5m/day=1 BM operates 0700 to 1,900	- 1 -	·+	2	-1	3AL1FT0858
Ten delegate of the first of th	- -	05JAN10 21J	15	TBM advances; Noise sesitive area CH1449-1295	3AL1FT0856
ABOOC I JUINZ AT DELICATION OF THE PROPERTY OF		20NOV09 04.JAN10	36		3AL1FT0854
ple-excevation evolution (9.20m/4.24m/6		13NOV09	9	TBM advances; F3 CH2255-2205	3AL1FT0852
SARDO I SILON SARDO SARD		29OCT09	13	TBM advances; CH2535-2255	3AL1FT0850
Dre-excevation grounding @ 20m/4 Edwar	28OCT09 1 8	21OCT09 28C	9		3AL1FT0848
	20OCT09 1 8	12OCT09 20C	80	-	3AL1FT0846
Dre-lexicavarian months (2) Dom (4 Educat	-	08OCT09 10C	(P)		3AL1FT0844
8.19.10.11.13.11.13.10.17.12.12.12.12.12.12.12.12.12.12.12.12.12.	T. 00T.		5	TBM advances; CH286	3AL1FT0842
TEMINAL SECTION DEFENDING THE CONDUCTION OF THE PROPERTY OF TH	any cal Total		δē		
TO STORE AND A STO	A STATE OF THE STA				O C

nud Activity Describition	Early Stan	Early. Cal Finish ID	Total D	POWER TOWN TO THE PROPERTY OF	A WIN TAKE OF
6AR1FT0932 6aR 16; On completion of grouting wks at F4	2	T09	1,062		0.0000000000000000000000000000000000000
6AR1FT0934 6aR 17; On completion of grouting wks at F3 0	-	19NOV09 2	1,040		
6AR1FT0936 6aR 18; On completion of grouting wks at F2 0	2	27JAN10 2	97.1	•	
	N I	27FEB10 2	940	•	
	-	13MAR10 2	926		
1	e	31MAR10 2	908		
	0		668	•	
6aR 23; On completion of	-	14APR10 2	894		
6aR 24; On completion of			888	•	
6aR 25; On completion of	2	710	885	•	,
F	2	28APR10 2	880	•	
6AR1FT0954 6aR 27; On completion of 70% grout by Ith at F1	· ·	04MAY10 2	874	•	
		10MAY10 2	898	•	
6AR1FT0958 6aR 29; On completion of 90% grout by Ith at F1 0	-	11MAY10 2	867	•	
6AR1FT0960 6aR 30; On completion of grouting works at F1	÷	14MAY10 2	864	•	
6AR1FT0970 6aR 31; On completion of all works under this CC 0	2	20MAY10 2	828	Sunder this Cast Centre	
न्यकाष्ट्रीया स्टाला Wilestrones to vegosts oenritestos saut					
3AL1FT1002 3aL 1; On providing evidence of procuring TBM 0		19JAN08 2	1,710	•	
3AL1FT1004 3aL 2; On providing evidence of TBM Factory Test 0	0	P08	1,481	•	
3AL1FT1006 3aL 3; On delivery of all parts of TBM to the Si	ŏ	09NOV08 2	1,415		
3AL1FT1008 3aL 4; On completion of site comm. & test. of TB 0	ð	800	1,386	•	
3AL1FT1010 3aL 5; On completion of 5% perm. tunnel lining	Š	25MAR09 2	1,279		
3AL1FT1012 3aL 6; On completion of 10% perm. tunnel lining 0	ŏ	09APR09 2	1,264	•	
3AL1FT1014 3aL 7; On completion of 15% perm. tunnel lining 0	ίδ.	22MAY09 2	1,22.1	•	
3AL1FT1016 3aL 8; On completion of 20% perm. tunnel lining 0	8	22JUN09 2	1,190	•	
3AL1FT1018 3aL 9; On completion of 25% perm. tunnel lining 0	_	10JUL09 2	1,172	•	
3AL1FT1020 :3aL 10; On completion of 30% perm. tunnel lining	α.	24JUL09 2	1,158	•	
3AL1FT1022 3aL 11; On completion of 35% perm. tunnel lining 0	1(L	1,141	•	
3AL1FT1024 3aL 12; On completion of 40% perm, tunnel lining 0	ŏ	09SEP09 2	1,1,1	•	
3aL 13; On completion of 45% perm. tunnel lining	ö		1,087	•	
	č.		1,066	•	
3AL1FT1030 3aL 15; On completion of 55% perm. tunnel lining 0	0	09NOV09 2	1,050	•	
3AL1FT1032 3aL 16; On completion of 60% perm. tunnel lining	2	27NOV09 2	1,032	•	
3AL1FT1034 3aL 17; On completion of 65% perm. tunnel lining	ŏ	CJ	1,020	•	
3AL1FT1036 3aL 18; On completion of 70% perm. tunnel lining	. 27	21DEC09 2	1,008	•	
3AL1FT1038 3aL 19; On completion of 75% perm. tunnel lining	72	22JAN10 2	926	•	
- 1	ð		362	•	
- 1	5	01MAR10 2	938	•	-
- T	Φ,		924	•	**
	0.	07APR10 2	901	•	
3AL1FT1048 3aL 24; On completion of perm. tunnel lining	4	14MAY10 2	864	•	
		ō			

	2 FO 1 - 4 O			
	03MAY08 27JUN12 1 24	1,230 03	108 Monitor/report Geotechnical Instrumentation	(SDCIAITIUS
	02MAY08 1	30 27		3DL1Al1106
	26MAR08 2 29	0	7	3DL1AI1104
	27MAR08 23JUN08 1 73	72 27	102 Tree transplanting; 4 nos.	16R7Al1102
	03MAY08 11JUL11 2 16	1,165 03	1	01R1AI1124
	27MAR08 02MAY08 1 12	30 27		01R1AI1122
	03MAY08 31MAY08 1 31	24		01R1AI117
	27MAR08 02MAY08 1 31	30 27	116 Site clearance	01R1AI1116
	27MAR08 02MAY08 1 31	30 27		01R1AI1114
◆90d after DOC	26MAR08 1 12	0 26	112 Possession of site	01R1A1112
	07MAR08 2 59	0 07		01R1AI1110
	26MAR08 2 90	0	108 Obtain tree felling permit	01R1AI1108
			Freinmany Works	
	A CONTRACT OF THE PROPERTY OF		Construction of Intake I-1	Const
 Tunnel after completion of strengtheing works 	18FEB09 2 1,314	0 du	T137 10aR 7; On recharge of the water after wrk comp	10AR1JT137
	•	0		10AR1JT136
	31JAN09 2 1,332	wks 0	- 1	10AR1JT135
	1	wks 0	T134 10aR 4; On completion of 50% strengthening wks	10AR1JT134
	20DEC08 2 1,374	wks 0	- 1	10AR1JT133
•	03DEC08 2 1,391	0		10AR1JT132
•	03DEC08 2 17,391	0	F-7	10AR1JT131
		035	Schealle of Miles (ones, Idrass) gentre Na (d	910S
under this Cost Centre ◆	26JUL12 2 60	0 00	1224 3dL 12; On completion of all works under this CC	3DL10T1224
flow mohitoring to issue of Main. Certificate.	26JUL12 2 60	O QV	- 1	3DL10T1222
flow measurement devices for Portion D.	19MAY11 2 . 494	0	- 1	3DL10T1220
flow measurement devices for Portion C.	05MAR11 2 569	0		3DL10T1218
flow measurement devices for Portion B.	10JUN11 2 472	0		3DL10T1216
flow measurement devices at Pontion A.	12MAR11 2 562	0		3DL10T1214
monitoring for installed i	26JUL12 2 60	0		3DL10T1212
installed instruments for 48 months from DOC.	26DEC11 2 273	0		3DL10T1210
Installed instruments for 36 months from DOC.	26DEC10 2 638	0		3DL10T1208
Installed Instruments for 24 months from DOC	1	0		3DL10T1206
Sinstalled instruments for 12 months from DOC	26DEC08 2 1,368	0		3DL10T1204
◆ gebtechnical instruments	02SEP09 2 1,118	0		3DL10T1202
◆within this cost centre	28JAN11 2 605	CC O	1034 3aL Z/; On completion of all works under this CC	3AL IF 1034
	01NOV10 2 693	nic. 0	7	3AL1FT1052
The part of Annual Control of the Co	24SEP10 2 731	han 0	-	3AL1FT1050
1 FM AMILE SEISOND TERMAMULTAS ON BEIERWAMITTES	Finish 10	Dar	200	
	Teld Total	BIO	S. WARM STATES	2

(

ç)	
4	č	
ć	Ķ)
1	į	į
ز	4	

OPR ANTACO Erect piling platform OPR INTEGRALIZE Erect piling platform 24 19JUN08 OPR IAM IZO4 Install 273 mm dia. temp. pipe piles; 175 nos. 36 18JUL00 11 REANI 208 360mm dia. per-bored H-piles; 66 nos. 36 29AUG08 11 REANI 308 Construct skin wall/access platforms; Portion A 72 20JUL10 4 LI REANI 308 Soil nailing at western side; 28 nos. 12 72JUN08 11 REANI 308 Soil nailing at western side; 120 nos. 24 17JUN08 11 REANI 308 Soil nailing at eastern side; 150 nos. 24 17JUN08 11 REANI 308 Soil nailing at eastern side; 150 nos. 24 17JUN08 11 REANI 308 Soil nailing at eastern side; 150 nos. 24 17JUN08 11 REANI 308 Soil nailing at eastern side; 150 nos. 24 15JUN08 20 LI Ald 40 Install working tie-back & proof load test; 1 no. 10 205EP08 20 LI Ald 40 Install working tie-back & proof load test; 1 no. 10 20NOV08 20 LI Ald 41 Bulk excavation; soil (550m3) 4 160ED08	17.JULO8 1 17 28AUGO8 1 17 24SEP10 1 198 24SEP10 1 198 31MAYO8 1 57 16JUNO8 1 57 15JULO8 1 57 15JULO8 1 17 12AUGO8 1 17 12NOVO8 1 17 12DECO8 1 17 11MARO9 1 17	Exercise to the containing AP for design submission Resoluting 7-day grout strength>30MPa Resoluting 7-day grout strength>30MPa
18		Rassuming 7-day grout strangth>30MPa
Excavation from +91.5mPD to + 88.5mPD 04L1Al1434 Bulk excavation; soil (1860m3) 18 12MAR09 04L1Al1436 Bulk excavation; rock (420m3) 18 26MAR09 04L1Al1440 Install working tie-backs; 27 nos. 12 26MAR09	12MAR09 01APR09 1 17 26MAR09 20APR09 1 17 26MAR09 07APR09 1 17 08APR09 24APR09 1 17	Est Ressuming 7-day grout istrength>30MPa

Excavation from +88.5mPD to +72.5mPD; North 04L1A11442 Bulk excavation; rock (6300m3) 07R1A11444 Bulk excavation for vehicular access; 1400m3 07R1A11446 Construct vehicular access Excavation to Bottom Level to south west of SR 04L1A11448 Bulk excavation; rock (5300m3) Construction of Spiral Ramp Structure 07R1A11402 Raft foundation 07R1A11404 Construct RC spiral ramp 07R1A11406 Construct RC spiral ramp ton	1 17	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1
	25APR09 04SEP09 1	
[]	30 01AUG09 04SEP09 1 17	SST ADOMS SECTION (Upper excavation)
Excavation to Bottom Level to south west of SR 04L1A11448 Bulk excavation; rock (5300m3) Construction of Spiral Ramp Structure 07R1A11402 Raft foundation 07R1A11404 Construct RC spiral ramp 07R1A11406 Construct RC spiral ramp ton	05SEP09 19OCT09 1	Fighton drote Extended of the order
04L1A11448 Bulk excavation; rock (5300m3) Construction of Spiral Ramp Structure 07R1A11402 Ratt foundation 07R1A11404 Construct RC spiral ramp 07R1A11406 Construct RC spiral ramp top		WALEST CALL STREET COLUMN STREET STRE
Construction of Spiral Ramp Structure 07R1Al1402 Raft foundation 07R1Al1404 Construct RC spiral ramp 07R1Al1406 Construct RC spiral ramp top	88 20OCT09 03FEB10 1 71	25.500 m 20.500 m 20.
		William Country of the Country of th
	12 20OCT09 03NOV09 1 17	Carbon Ca
	Ž	=10272m2, re-bar=755f. condrete=2788m3程列码器
İ	12 02JUL10 15JUL10 1 17	MADOW STATE OF THE
Dismantle & removal of TBM		OHIOTO
04L1Al1450 Install temporary steel works for removal of TBM	24 16APR10 14MAY10 1 17	E
04L1Al1452 Dissembly & demobilization of TBM	15MAY10 15JUL10 1	ECCLEGE STATE OF THE STATE OF T
Construction of Cascade Structure	.1	AVECTOR AND ADDRESS OF THE PROPERTY OF THE PRO
04L1Al1454 Construct box culvert & cascade	72 16JUL10 09OCT10 1 17	fwke 880m2 re-har-145t & Annersta-049m2898988 &
Mod frattonati atsung Chamelinany sessor		
OTETATENT Medits chemen had 0	AND THE PROPERTY OF THE PROPER	
T	01NOV10" 11DEC10 1	
Modify channel bed and orlice; Phase	13DEC10	
07R1Al1506 Modify channel bed and orfice; Phase 3	36 27JAN11 12MAR11 1 61	
Remaining Works Proprietaver		
07R1AI1602 Backfill & compaction above box culvert; Port. A	72 11OCT10 06.IAN11 1 90	T. C.
07B1Al1606 Finishing & reinstatement works; Portion A	14FEB11 11APR11 1	POST TO THE POST T
07R1Al1608 Pre-handover inspections and remedial works	14MAB11 13MAY11 1	Total Carlo
07R1Al1610 Contractor serve notice for Works completion	14MAY11 20MAY11 2 4	
07R1A11612 SO issues completion certificate	10JUN11 2	
	13MAY11 1	15000s climber 20000s world and 20000s and 20000s
16R7Al1604 Establishment Works at Portion A	365 14MAY11 12MAY12 2 75	
3DL1AI1602 Install flow measurement devices at Intake I-1	12MAR11 1	
3DL1AI1604 Maintain & monitor flow monitoring	365 13MAR11 11MAR12 2 137	
Suiçonie of fulles for established at		
04L1Al1802 4L 1; On completion of 50% excavation	0 24APBng 2 1.249	A CONTRACTOR OF THE PROPERTY O
04L1Al1804 4L 2; On completion of excavation	03FEB10 2	Tot Castal at this of the Control of this of the Control of the Co
04L1A11806 4L 3; On completion of 25% concreting	2	October 1 Hare 1-1
04L1Al1808 4L 4; On completion of 50% concreting	0 26AUG10 2 760	Pro Cascade at Intake 1-1
	0 16SEP10 2 739	• for Cascade at Intake 1-1
[0 09OCT10 2 716	• Patiniake III
i	0 19OCT09 2 1,071	Spox culvert at Intake I-1
04L1Al1816 4L 8; On completion of all works under this CC	0 13MAY11 2 500	entrantic Cost

Fig.	778 1. On completion of trash guile 778 2. On completion of 25% excertainth 2 265 778 2. On completion of 25% excertainth 2 205 2 255 2 255 2 2 2 2	Start. Finish 10. Fisal 18.9	
The 1-Concentration of 15% executation	778 (1.00 completion of treat) guils 778 (1.00 completion of treat) guils 778 (1.00 completion of 12% excavation 0 12MAR10 2 1.365		sienesifor@sk.cemte.Nor7R
778 ± Cho completion of Side accessarion 0 200ECG 2 3.555 4 spiral armo al lunde in H 1 1 1 1 1 1 1 1 1	778 Ch completion of 25% excavation	2 562	
77.8 Concompletion of Size securation 0 C2LMAR10 2 1.220 77.8 Concompletion of Size securation 0 C2LMAR10 2 1.120 77.8 Concompletion of Size securation 0 C2LMAR10 2 1.120 77.8 Concompletion of Size securation 0 C2LMAR10 2 1.120 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 C2LMAR10 2 357 77.8 Concompletion of Size securation 0 C2LMAR10 C2LMAR10 2 374 77.8 Concompletion of Size securation 0 C2LMAR10 C2LMA	This 4.0 normpletion of 50% excertaint 0 11MA/102 2 1.250 This 2.0 normpletion of 50% excertaint 0 0 0.045EPD0 2.116 This 2.0 normpletion of sprial ramp to +80mPD 0 0.045EPD0 2.116 This 2.0 normpletion of sprial ramp to +80mPD 0 0.045EPD0 2.116 This 2.0 normpletion of sprial ramp to +80mPD 0 0.045EPD0 2.106 This 2.0 normpletion of sprial ramp to +100mPD 0 1.10MA/10 2.805 This 3.0 normpletion of sprial ramp to +100mPD 0 1.10MA/10 2.805 This 3.0 normpletion of sprial ramp to +100mPD 0 1.10MA/10 2.805 This 3.0 normpletion of sprial ramp to +100mPD 0 1.10MA/10 2.805 This 3.0 normpletion of sprial ramp to +100mPD 0 1.10MA/10 2.805 This 3.0 normpletion of sprial ramp to +100mPD 0 1.10MA/10 2.805 This 3.0 normpletion of sprial ramp to +100mPD 0 1.10MA/10 2.805 This 3.0 normpletion of sprial ramp to +100mPD 0 1.10MA/10 2.704 This 3.0 normpletion of sprial ramp to +100mPD 0 2.445EP10 2.704 This 3.0 normpletion of sprial ramp to +100mPD 0 2.445EP10 2.704 This 3.0 normpletion of sprial ramp to +100mPD 0 2.445EP10 2.704 This 3.0 normpletion of sprial ramp to +100mPD 0 2.445EP10 2.704 This 3.0 normpletion of sprial ramp to +100mPD 0 2.445EP10 2.704 This 3.0 normpletion of sprial ramp to +100mPD 0 2.445EP10 2.704 This 3.0 normpletion of sprial ramp to +100mPD 0 2.844AR0 2.104 The 4.0 normpletion of sprial ramp to +100mPD 0 2.844AR0 2.104 The 4.0 normpletion of sprial ramp to +100mPD 0 2.844AR0 2.104 The 4.0 normpletion of sprial ramp to +100mPD 0 2.844AR0 2.104 The 4.0 normpletion of sprial ramp to +100mPD 0 2.844AR0 2.104 The 4.0 normpletion of sprial ramp to +100mPD 0 2.844AR0 2.104 The 4.0 normpletion of sprial ramp to +100mPD 0 2.844AR0 2.104 This 3.0 normpletion of sprial ramp to +100mPD 0 2.844AR0 0 2.448AR0 0 2.104 This 3.0 normpletion of s	2 1,365	
The 2-to completion of size accessions 0 0 0 0 0 0	The 2-to completion of standard and to +80mPD 0 02JMV09 2 1/16 0 040m	2 1,293	
77 B. Cho completion of signal armoto at Intake 1-1 77 B. Cho completion of signal armoto be -36m-70 77 Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto be -36m-70 77 B. Cho completion of signal armoto armoto be -36m-70 77 B. Cho completion of signal armoto armoto be -36m-70 77 B. Cho completion of signal armoto armoto be -36m-70 77 B. Cho completion of signal armoto armoto be -36m-70 77 B. Cho completion of signal armoto armoto be -36m-70 77 B. Cho completion of signal armoto armo	77 B; Ch completion of sprial ramp to ±60mPD	2 1,210	
This Concompletion of spiral transp to schemb	The 2, On completion of spiral amp to +30mPD	2 1,116	
77 R (2.0) compeletor of sprial ramp to +30nPD 0 0204/410 2 867 77 R (2.0) compeletor of sprial ramp to +30nPD 0 1504/10 2 868 77 R (2.0) compeletor of sprial ramp to 100nPD 0 1504/10 2 868 77 R (2.0) compeletor of sprial ramp to 100nPD 0 1704/10 2 868 77 R (2.0) compeletor of sprial ramp and this collection of particular sprials are considered of sprial ramp and this collection of particular sprials are considered of sprial ramp and this collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials ramp collection of particular sprials are considered of sprials are considered of sprials are considered of sprials are considered of sprials are collection of sprials are considered or spr	TR 8; On completion of spiral camp to +50mPO	2 1,007	
778 (2) On completion of spiral amplies a spiral amplies of spiral amplies and spiral amplies amplies and spiral amplies and	778 c. On completion of spiral ramp to ±100mPD	2 937	
778 (2) On completion of spiral access amp 134,011 2 500 78 (10 Completion of spiral access amp 134,011 2 500 78 (10 Completion of spiral access to the part of the	178 9; On completion of spiral access ramp 0 15AUL10 2 802 178 1; On completion of sil works under this CO 0 15AUL10 2 802 178 2; On completion of sil works under this CO 0 15AUL10 2 1500 178 2; On completion of sil works under this CO 0 15AUL10 2 1540 178 3; On completion of sil works under this CO 0 15AUL10 2 1542 178 3; On completion of sil works under this CO 0 25AUR10 2 1542 178 4; On completion of sil works under this CO 0 25AUR10 2 1542 178 4; On completion of sil works under this CO 0 25AUR10 2 1542 178 4; On completion of sil works under this CO 0 25AUR10 2 1542 178 4; On completion of sil works under this CO 0 25AUR10 2 1542 188 5; On completion of sil works under this CO 0 25AUR10 2 1542 188 6; On completion of sil works under this CO 0 25AUR10 2 1542 188 6; On completion of sil works under this CO 0 25AUR10 2 1542 189 6; On completion of sil works under this CO 0 25AUR10 2 1542 189 6; On completion of sil works under this CO 0 25AUR10 2 1542 189 6; On completion of sil works under this CO 0 25AUR10 2 1542 189 6; On completion of sil works under this CO 0 25AUR10 2 1542 189 6; On completion of sil works under this CO 25AUR10 2 1542 189 6; On completion of sil works under this CO 25AUR10 2 1542 189 6; On completion of sil works under this CO 25AUR10 2 1542 189 6; On completion of sil works under this CO 25AUR10 2 1542 189 6; On completion of sil works under this CO 25AUR10 2 1542 189 6; On completion of sil works under this CO 25AUR10 2 200 189 6; On completion of sil works under this CO 25AUR10 2 200 189 6; On completion of sil works under this CO 25AUR10 2 200 189 6; On completion of sil works under this cooles ramp along west side of stream 25AUR10 2 200 180 6; On completion of sil works under this cooles ra	2 868	
11 R 1, Ch completion of all works under this CC 0 13MAY11 2 500 4 thinks 1 1 1 1 1 1 1 1 1	11R 1: On completion of all works under this CC	2 · 802	
11R 1; On completion of sail rading works 0 12ALIGOB 2 1504 11R 2; On completion of sail rading works 0 13SEPDB 2 1504 11R 2; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 3; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 13SEPDB 2 1442 11R 4; On completion of pling at brainch access 0 1442 11R 4; On completion of pling at brainch access 0 1442 11R 4; On completion of pling at part plant 0 1442 11R 4; On completion of pling at part plant 0 1442 11R 4; On completion of pling at part plant 0 1442 11R 4; On completion of pling at part plant 0 1442 11R 4; On completion of pling at part plant 0 1442 11R 4; On completion of pling at part plant 0 1442 11R 4; On completion of pling at part plant 0 1442 11R 5; On completion of pling at part plant 0 1442 11R 5; On completion of pling at part plant 0 1442 11R 5; On completion of plant 0 1442 11R 5; On completion access camp plant 0	11R 2; On completion of soling works 1	2 500	8
11R 2: On completion of soin railing works 0 12ALIOSB 2 1.6504	11R 1; On completion of piling works 0 19SEP08 2 1,566		sionestor Gast Centrello Itil
11ff 2; On completion of piling at bianch access 0 185EPOS 2 1,442	11R3 Con completion of piling at platform 0 18SEP08 2 1,446 4 4 4 4 4 4 4 4 4	2 1 504	
11R 3: On completion of pling at branch access of one of the completion of pling at branch access a intike I-1 11R 4: On completion of pling at branch access a intike I-1 11R 5: On completion of pling at branch access a intike I-1 11R 5: On completion of pling at branch access a intike I-1 11R 5: On completion of all works under this OC	11R 4; On completion of piling at baranch access a final file of the control peling at baranch access a final file of the control peling at baranch access a final file of the control peling at baranch access a final file of the control peling at baranch access and the control peling at baranch access and the control peling at baranch access and the control peling at set the con	2 1.466	
11R 4; On completion of all works under this CC	118.4; On completion of all works under this CC	1 440	access
Obtain TTA (ingress & egress) approval 0 28MAR08 2 36	Obtain TTA (ingress & egress) approval	20 2 731	
Cobtain TTA (ingress & egress) approval 0 26MAR08 2 36 4 4 4 4 4 4 4 4 4	Obtain TTA (ingress & egress) approval		
Dobain TTA (ingress & egress) approval by Cossession of Portion B and of DOC	Dobtain TTA (frogress & egrees) approval 0 26MAR08 2 15 4 Possession of Portion B -90d of DOC 0 26MAR08 2 15 Site establishment 30 27MAR08 02MAY08 1 13 Install remote control CCTV as per ER 4.4.10 30 27MAR08 02MAY08 1 12 Maintain & operate CCTV 1.165 03MAY08 1.1UL1 2 16 Installation of Geotechnical Instrumentation 1,230 03MAY08 1.1UL1 2 16 Installation of Geotechnical Instrumentation 1,230 03MAY08 1 13 Installation of Geotechnical Holies 1 15,UL08 1 298 Installation of Fire of Stream 1 15,UL08 1 298 Installation of Fire of Stream 1 15,UL08 1 298 Installation of Fire of Stream 1 15,UL08 1 298 Installation of Fire of Stream 1 15,UL08 1 298 Installation of Fire of Stream 1 15,UL08 1 298 Installation of Fire of Stream 1 15,UL08 1 298 Installation of Fire of Stream 1 1 1 1 1 1 1 1 1		make I+2 S
Site establishment Site es	Possession of Portion B -90d of DOC 0 26MAR08 2 15 45	2 36	
Site establishment 30 27AAR08 CAMAYOB 1 13 EE EE <t< td=""><td>Site dearance 30 27MAR08 02MAY08 1 13 Install remote control CCTV as per ER 44.10 30 27MAR08 02MAY08 1 12 Maintain & operate CCTV 1,165 03MAY08 1 1,111 2 16 Tree transplanting; 1 no. 72 03APR08 30,UMV08 1 38 Obtain approval for Geotechnical Instrumentation 30 27MAR08 02MAY08 1 34 Monitor/report Geotechnical Instrumentation 30 27MAR08 27JUN12 1 24 Monitor/report Geotechnical Instrumentation 1,230 03MAY08 27JUN12 1 24 Monitor/report Geotechnical Instrumentation 1,230 03MAY08 27JUN12 1 24 Monitor/report Geotechnical Instrumentation 24 05APR08 03MAY08 1 13 Monitor/report Geotechnical Instrumentation 6 05MAY08 1 13 6 Form temp. access ramp along west side of stream 24 6 05MAY08 1 1 15 nos</td><td>2 15</td><td>0</td></t<>	Site dearance 30 27MAR08 02MAY08 1 13 Install remote control CCTV as per ER 44.10 30 27MAR08 02MAY08 1 12 Maintain & operate CCTV 1,165 03MAY08 1 1,111 2 16 Tree transplanting; 1 no. 72 03APR08 30,UMV08 1 38 Obtain approval for Geotechnical Instrumentation 30 27MAR08 02MAY08 1 34 Monitor/report Geotechnical Instrumentation 30 27MAR08 27JUN12 1 24 Monitor/report Geotechnical Instrumentation 1,230 03MAY08 27JUN12 1 24 Monitor/report Geotechnical Instrumentation 1,230 03MAY08 27JUN12 1 24 Monitor/report Geotechnical Instrumentation 24 05APR08 03MAY08 1 13 Monitor/report Geotechnical Instrumentation 6 05MAY08 1 13 6 Form temp. access ramp along west side of stream 24 6 05MAY08 1 1 15 nos	2 15	0
Site clearance	Site clearance	02MAY08 1 13	30
Install remote contorl CCTV as per ER 4.4.10 30 27MAR08 02MAY08 1 12 Maintain & operate CCTV 1,165 03MAY08 1,10L1 2 16 Maintain & operate CCTV 1,165 03MAY08 1,10L1 2 16 Maintain & operate CCTV 1,165 03MAY08 1,10L1 2 16 Maintain & operate CCTV 1,165 03MAY08 1,10L1 2 16 Maintain & operate CCTV 1,165 03MAY08 1,10L1 2 16 Maintain & operate CCTV 1,165 03MAY08 1,10L1 2 1,10 Maintain & operate CCTV 1,10 1,	Install remote control CCTV as per ER 4.4.10 30 27MAR08 02MAY08 1 12 ER 4.4.10 1.165 03MAY08 1.1UL1 2 16 ER 4.4.10 1.165 03MAY08 1.1UL1 2 16 ER 4.4.10 1.165 03MAY08 1.1UL1 2 16 ER 4.4.10 1.105 03MAY08 1.1UL1 2 16 ER 4.4.10 1.105 0.2MAR08 1 1.3 ER 4.4.10 1.2 0.2MAR08 1 1.3 ER 4.4.10 ER 4.4.1	708 1 13	30
Maintain & operate CCTV 1,165 03MAY08 11JUL11 2 16 15 16	Maintain & operate CCTV	02MAY08 1 12	30
Tree transplanting: 1 no. 72 03APR08 30JUN08 1 398	Tree transplanting: 1 no. 72 03APR08 30JUN08 1 398	11JUL11 2 16	1,165
Obtain approval for Geotechnical Instrumentation 0 26MAR08 2 16	Obtain approval for Geotechnical Instrumentation 0 26MAR08 2 16	30JUN08 1 398	72
Installation of Geotechnical Instrumentation 30 27MAR08 02MAY08 1 13 EFFECTION	Installation of Geotechnical Instrumentation 30 27MAR08 02MAY08 1 13 EFFECTION	2	
Wonitor/report Geotechnical Instrumentation 1,230 03MAY08 27JUN12 1 24 CAPRON 05APRON 13 With the implementation of TTA Gost Local Labele Stream access ramp along west side of stream 24 05APRON 03MAY08 1 13 with the implementation of TTA Homolize piling rig & set up 6 05MAY08 10MAY08 1 13 with the implementation of TTA 15 nos. pre-bored H-piles at southern access ramp (tail) 12 24MAY08 05JUN08 14JUL08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 15JUL08 1 298 Demolize piling rig 1 15JUL08 1 298 Excavate for skin wall & remove lemp, access 40 16JUL08 1 298 Excavate for skin wall & remove lemp, access 40 16JUL08 1 298 Excavate for skin wall & remove lemp, access 40 16JUL08 1 298 Excavate for skin wall & remove lemp, access 40 16JUL08 1 298 Excavate for skin wall & remove lemp, access 40 16JUL08 1	Wonitor/report Geotechnical Instrumentation 1,230 03MAY08 27JUN12 1 24 CAPRON 23MAY08 1 33MAY08 1 33MAY08 1 33MAY08 1 33MAY08 1 33MAY08 1 13 4mith the implementation of TTA Hermation of A ros. pre-bored H-piles at southern end Southern access ramp (tail) 12 24MAY08 05JUN08 1 13 4mith the implementation of TTA Remaining 44 nos. pre-bored H-piles at southern access ramp (tail) 12 24MAY08 05JUN08 1 13 6milling rig Demolize piling rig 1 15JUL08 1 298 6milling rig 6milling rig	02MAY08 1 13	30 27MAR08
Gardia. H-Pile Wall Form temp, access ramp along west side of stream 24 05APR08 03MAY08 1 13 Mobilize piling rig & set up 6 05MAY08 10MAY08 1 13 15 nos. pre-bored H-piles at southern access ramp (tail) 12 24MAY08 05JUN08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	Gardia. H-Pile Wall Form temp, access ramp along west side of stream 24 05APR08 03MAY08 1 13 Mobilize piling rig & set up 6 05MAY08 10MAY08 1 13 15 nos. pre-bored H-piles at southern end 10 13MAY08 23MAY08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 1 13 Demolize piling rig 1 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	273UN12 1 24	
g 1-Construct 550 dia. H-Pile Wail 24 05APR08 03MAY08 1 13 Mobilize piling rig & set up 6 05MAY08 1 13 15 nos. pre-bored H-piles at southern end 10 13MAY08 23MAY08 1 13 Remove southern access ramp (tail) 12 24MAY08 06JUN08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	g 1-Construct 550 dia. H-Pile Wail 24 05APR08 03MAY08 1 13 Mobilize piling rig & set up 6 05MAY08 1 13 15 nos. pre-bored H-piles at southern end 10 13MAY08 23MAY08 1 13 Remove southern access ramp (tail) 12 24MAY08 06JUN08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove termp, access 40 16JUL08 30AUG08 1 298		Appreading in annel Health Wall
Form temp, access ramp along west side of stream 24 05APR06 03MAY08 1 13 Mobilize piling rig & set up 6 05MAY08 10MAY08 1 13 15 nos. pre-bored H-piles at southern end 10 13MAY08 23MAY08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 1 13 Demolize piling rig 1 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	Form temp, access ramp along west side of stream 24 05APR06 03MAY08 1 13 Mobilize piling rig & set up 6 05MAY08 10MAY08 1 13 15 nos. pre-bored H-piles at southern end 10 13MAY08 23MAY08 1 13 Remove southern access ramp (tail) 12 24MAY08 06JUN08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298		truct 550 dia. H-Pile Wali
Mobilize piling rig & set up 6 05MaY08 1 0MaY08 1 13 15 nos. pre-bored H-piles at southern end 10 13MaY08 23MaY08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 1 298	Mobilize piling rig & set up 6 05MaY08 1 0MaY08 1 13 15 nos. pre-bored H-piles at southern end 10 13MaY08 23MaY08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove termp, access 40 16JUL08 1 298	03MAY08 1	24 05APR08
15 nos. pre-bored H-piles at southern end 10 13MAY08 22MAY08 1 13 Remove southern access ramp (tail) 12 24MAY08 06JUN08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 1 298 Excavate for skin wall & remove temp. access 40 16JUL08 1 298	15 nos. pre-bored H-piles at southern end 10 13MAY08 22MAY08 1 13 Remave southern access ramp (tail) 12 24MAY08 06JUN08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 1 298	10MAY08 1 13	Ø
Remove southern access ramp (tail) 12 24MAY08 06JUN08 1 13 Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	Remove southern access ramp (tail) 12 24MAY08 06.UN08 1 13 Remaining 44 nos. pre-bored H-piles 30 07.UN08 14.UU.08 1 298 Demolize piling rig 1 15.UL.08 1 298 Excavate for skin wall & remove temp, access 40 16.UL.08 1 298	23MAY08 1 13	10
Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove temp. access 40 16JUL08 1 298	Remaining 44 nos. pre-bored H-piles 30 07JUN08 14JUL08 1 298 Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove temp. access 40 16JUL08 30AUG08 1 298	06JUN08 1 13	12
Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	Demolize piling rig 1 15JUL08 15JUL08 1 298 Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	14JUL08 1 298	30
Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	Excavate for skin wall & remove temp, access 40 16JUL08 30AUG08 1 298	15JUL08 1 298	
		30AUG08 1 298	40

42
ō
9
eet
돐

12R3Bl2216 Construct skin walf; 45m; Portion B	_	8.9.1011/21014/1918/1019/2020/2020/2020/2020/2020/2020/2020
Phase 1, Stg 3-Flatten exist. Stream Red at West	200000000000000000000000000000000000000	
Construct temp. concrete block bund	12 01NDV08* 14NDV08 1	
Excavate for new low flow channel	15NOV08 : 28NOV08 1 236	-provision of water pump
Construct new low flow channel	29NOV08 29DEC08 1 236	
Remove temp, concrete block bund	30DEC08 13JAN09 1 236	
Phase 2, Stg 1- Const. Approach Channel at East		
Construct temp, concrete block bund	6 02NOV09* 07NOV09 1 0	
Excavate for L-shaped retaining wall	09NOV09 21NOV09 1	provision of water pump
Construct L-shaped retaining wall	, 18 Z3NOV09 12DEC09 1 175	
Excavate eastern portion of guide wall & slab	29DEC09 1	
Construct eastern portion of guide wall & slab	20JAN10 1	
Remove temp, concrete blook bund	27JAN10 1	
Phase 2, Stg 2- Const Approach Channel at West		
Construct temp, concrete block bund	8 28 IANIO DAEERIO 4 17E	
Excavate for western portion guide wall & slab	+	Eprovision of water pump
Construct western portion of guide wall & stab	22FFB10 20MAB10 1	
Remove concrete block bund	22MAR10	E .
Phase 4- Construct Remaining Approach Channel		3
Construct temp, concrete block bund	6 18APR11 27APR11 1 8	3
Complete guide wall between A.C. & V.S.	12MAY11 1	ž ž
Remove temp. conctete block bund	6 13MAY11 19MAY11 1 8	*After Construction of Outfall O-1
Excevate greensimor Veltexibrop Shaft		
Phase 1, Stg 2- Form temp. access ramp to VS		
Setting up	6 05SEP08 11SEP08 1 13	
Probing & curtain grouting around shaft	12SEP08 13OCT08 1 13	
Construct ELS around shaft	03NOV08 1 13	
Phase 3, Stg 1- Const. Vortex Shaft/Trash Grill		
Construct temp. concrete block bund	6 01NOV10* 06NOV10 1 0	
Excavate for vortex shaft & guide wall	24 27NOV10 24DEC10 1 13	provision of water bump
Construct vortex shaft & guide wall		
Construct trash grill		1000
Construction of boulder traps; 7nos.	-	S .
Phase 3, Stg 2- Construct Rem. West. Guide Wall		
Relocate temp, concrete block bund	4 12MAR11 16MAR11 1 13	у
Excavate/const. rem. western guide wall		
Remove temp, concrete block bund	-	
Mechanical expanation for dron shaft 32m		
Construct door at all 100	13	Managarata @ 0.2m/day
Cristian Crop shaft: 3.4m		

	T Caro	יייייייייייייייייייייייייייייייייייייי	
	365 17JUL11 15JUL12 2 11	Establishment Works at Portion B	16R7BI2104
Projection:		Landscaping works at Portion B	16R7BI2102
	21 24JUL11 13AUG11 2 348	SO issues completion certificate	08R1BI2105
	17JUL11	Contractor serve notice for Works completion	08R1BI2104
Manager Control of the Control of th		Pre-handover inspections and remedial works	08R1BI2103
	48 18APR11 17JUN11 1 8	Finishing & reinstatement works; Portion B	08R1Bl2102
		Renizintig Warks Pridric Handover)
5 bays, invert, walls & toof 3 pours each bay感动	36 27NOV10 11JAN11 1 38	Construct man access tunnel; 35m	051.1812806
	30AUG10	Mechanical excavation breakthrough	05L1BI2804
国の表示の記念の記念の記念 @ 0.15m/day	240 06NOV09 28AUG10 1 109	Mechanical excavation for Man Access Tunnel	05L1BI2802
		excevere woonshippen access hunde	
(認証(ryert, wall & ropf	36 26JAN11 11MAR11 1 38	Construct collar between MT & AT	3BL1B12108
18@ 0,3m/day	25JAN11 1	Mechanical excavation breakthrough	3BL1BI2106
Marie Bays, Invert, walls & roof 8 pours @ bay 51 d	50 14JUL10 09SEP10 1 13	Construct adit tunnel; 60m	3BL1Bl2104
SESTING SESTION © 0.3m/day	200 06NOV09 13JUL10 1 13	Mechanical excavation for Adit Tunnel	3811812102
		Excavate o Gonstruct Aul Funnell	EX(0.01/2)
IIIII 2 walls & roof total 32 days	32 10SEP10 20OCT10 1 13	Construct de-aeration chamber	05L1BI2604
2832m3, 2@ 20m3/day	132 01JUN09 05NOV09 1 13	Mechanical excavation for chamber; 22.5m	051,1812602
		encevare a construction deferration oranides	(*) (*) (*)
EGATING 4m/8days	76 27NOV10 02MAR11 1 67	Construct man access shaft including stairs; 38m	05L1Bl2514
Exercise Control of Smiday	190 30DEC08 21AUG09 1 443	Mechanical excavation for man access shaft; 38m	05L1BI2512
	24 29NOV08 29DEC08 1 443	Probing & curtain grouting around shaft	051.1812504
₹335mm dfa. temp. pipe pile wall	24 01NOV08* 28NOV08 1 0	Construct ELS around shaft	0511812502
		Excavate Goostfloot/Nart Access Shaff	
©a [®] @4m/4days	34 27NOV10 08JAN11 1 67	Construct air vent shaft; 34m	3BL1B12412
	6 04NOV08 10NOV08 1 13	Dismante & remove temp platform	05L1BI2410
provision of TTA	1 04SEP08 04SEP08 1 13	Demobilize RCD	05L1B12408
图 图	34 26JUL08 03SEP08 1 13	Excavate by RCD; 34m @ 1m/day	05L1BI2406
Provision of TTA	6 19JUL08 25JUL08 1 13	Mobilize & set up plants for RCD excavation	05L1BI2404
	10 08JUL08 18JUL08 1 13	Construct temp. platform for RCD	05L1BI2402
	24 07JUN08 07JUL08 1 13	Form temp, access ramp; Lo Wai Rd to Drop Shaft	05L1BI2302
		Phase 1, Stg 2- Form temp. access ramp to VS	Phase 1, St
		Szodyaler z Gönstrubt Arriventshaft	The system
FINA MELTAN BOND BUTEN AND TO BE BOND TO BE BUTEN TO BE BUTEN AND THE MACKED ONE OF THE MACKED WESTED OF THE BUTEN AND THE MACKED WESTED ONE OF THE BUTEN AND THE BUTEN	7.0	Description	9
	Fant Cal Total	Allowy	9

•under this Cost Centre			16JUL11	0	12114, Oil completion of all works under this CC
◆traps at Intake -2		2	11MAR11	0	12R3bl2Sub 12R 3; On completion of boulder traps
	wall at Intake I-2	13SEP08 2 1,472	13SE	0	Ţ.
	♦wall at Intake I-2	14JUL08 2 1,533	14.11	0	\Box T
♦under this Cost Centre		16JUL11 2 436	16J	0	CONTROLL TO GARAS, OF COMPREHEND OF All WORKS UNder This CC
Aat Intake I-2			25FI	0	U8K1 BI2R04 8R 2; On completion of trash grill
channel and assiciated decking at fritake 1-2.	chan	AY11 2 501	12MA	0	
◆under this Cost Centre		JL11 2 436	1630	O T	The sample of th
◆adit at Intake F-2		2	011	0	OF TRIOMOD RI 10: On completion of all marks and
Shaft at Intake I-2		~	02M	0	OSE REIGHTE SE 8; On completion of man access shaft
C.I. extrait at interest		08JAN11 2 625	08)	0	
Chambar at Intake 1.2		200CT10 2 705	200	0	
Programme and the second secon			114	0	
Second Cit. except for Adit at Intake 1.2		2	28A	0	T
Z-laving at line to the control of		09MAR10 2 930	M60	0	1
The properties of the properti		14SEP09 2 1,106	148	0	T
On Moleculary of Land and the Author of Land and		30MAY09 2 1,213	300	0	
					Shearle o Miestoresia cos centre Na El
S-I Preside the Control of the Contr	-114.4	AR11 2 563	11MA	0	35t.1 bizAzu 35L 10; On completion of all works under this CC
for Ach Timpol of Intolo 15		P10 2	3S60	0	- 7.
Fron Adil Turnel at Intake 1-2	- 18	P10 2	028E	0	1
Tor Adit Tunnel at Intake 1-2	- V (pr.	310 : 2	26AU	0	-
Tor Adit Tunnel at Intake 1-2		310 2	19AU	0	
Tor Adit Tunnellat Intake I-2		310 2	11AIK	0	
▼1or Adit Tunnel at Intake I-2		G10 2	04AU	0	_
		110 2	UL/2	0	7
equipment so tunnelling at Intake I-2		2	20,	O	
Committee of the second of the		05NOV09 2 1,054	Į,	0	-
			1		
	· · · · · · · · · · · · · · · · · · ·	1415 2		CONTRACTOR OF STREET	
mvo.		1 IN 14 0		THE STATE OF THE S	3
			11JUN11	365	3DL1BI2105 Maintain & monitor flow monitoring

	ABINITY DESCRIPTION	Ong Early Dur Stan	Early Cal Total Finish ID Float	DILIEMANIA ITAISON DULEMANIA MANGOLINE DILIEMANIA ILANSON DULE MANDULA MANDULA MANDULA MANDULA MANDULA MANDULA 78 BIOOTII II INTERNATION DULEMANIA MANDULA MANDULANIA MANDULA MANDULA MANDULA MANDULA MANDULA MANDULA MANDULA
	Sousinging tower part of Abress Hoad			
09R1Cl3402	1 [60 13MAY09	09 23JUL09 1 274	
09R1Cl3406		60 24JUL09	02OCT09 1	
09R1CI3408	ı	30 03OCT	03OCT09 09NOV09 1 274	
09R1CI3410		32 10NOV(-	
09R1Cl3412		32 17DECC	4N10 1	
09R1Cl3414	1	48 27JAN10	-	
13R1CI3402		112 28AUGC	28AUG08 12JAN09 1 288	
13R1Cl3404	Excavate & install soil nail (NW Turning Area)		-	Con Colonia 100 Colonia
13R1Cl3406		+	12MAY09 1	Manager Control Cont
16R7CI3402		 -	24FEB09 1	COLLINGIA DE LA COLLINGIA DE L
Excenden	excayate & constitution of New Shares			
Phase 1	AND THE RESIDENCE OF THE PROPERTY OF THE PROPE			
06L1Cl3502	Modify & flatten the stream bed	6 26NOV08	02DFC08 1	
06L1CI3504	-	1	· 🛉	
06L1Cl3506	Γ	+		
06L1Cl3508		+ .	20JAN09 1	MATTER OF THE CONTRACT OF THE
06L1Cl3510	Construction of air vent shaft	14 21JAN09	09FEB09 1 1	
eyib Neoxal	Excavate seconstruction of a share			The control of taken by the control of the control
Phase 1			POPULATION OF THE PROPERTY OF	
06L1Cl3602		18 21 JAN09	9 13FEB09 1 71	
06L1Cl3604		24 21JAN0	20FEB09 1	
06L1Cl3606	-7	57 14FEB0	14FEB09 25APR09 1 71	(2000年1136m3,10m3*b/dav= 57
06L1CI3608	Bulk excavation for drop shaft	60 27APH09	9 09JUL09 1 71	
06L1Cl3610	Construction of vortex (southern portion)	24 10JUL09	9 06AUG09 1 71	
Phase 2				
06L1Cl3612	Construction of drop shaft	12 19FEB10 04MA	0 04MAR10 1 83	B@4m/4clavs
Phase 3				
06L1Cl3614	Bulk excavation for Vortex (northern portion)	37 21SEP1(21SEP10 05NOV10 1 106	70 - White Holl 10 marks 10 m
06L1Cl3616	Construction of vortex (northern portion)	24 06NOV10 03DE	C10	SEE AND COLLEGE OF THE
06L1Cl3618	Relocate flood wall within vortex	4 04DEC10	C10 1	
06L1Cl3620	Construct remaining of the vortex	24 09DEC10	08JAN11 1	
21	8 oonsiidei Mar Access Shelf			
Phase 1				
06L1Cl3706	Bulk excavation for man access shaft	110 14FEB09	9 30JUN09 1 170	Waterway (a) 2m/dav
06L1Cl3708	Construction of man access shaft	44 30SEP09	9 23NOV09 1 170	6*4 cycle each cycle 4 days部型22m @ 4m/8days inclinating stairs
Metal Mean	Weldinganorsingam Belti (by Seasonnik)			
Phase 2	AN AND AND AN			
09R1Cl3802	Construct temporary sand bag bund	6 02NOV09* 07NO	1 07NOV09 1 0	

09R1CI3804 09R1CI3806 09R1CI3808		THE PARTY NAMED IN			1031 7 8 9	
09R1CI3806 09R1CI3808 09R1CI3810	Removal of large boulders	01	60AON60	19NOV09		88.9 P. 01.11.21.31.41.51.61.77.08 P. 92021 P. 22021 P. 2
09R1CI3808 09R1CI3810	Excavation of the stream bed	36	20NOV09		1 67	2
09R1Cl3810	Laying of granular filter	42	05JAN10	05JAN10 01FEB10	16	
(T (C () T () () T () T	Laying of rock armour	24	05JAN10	05JAN10 · 01FEB10	1 67	
09R1CI3812	Construction of boulder trap; 7 nos.	24	02FEB10	04MAR10	1 67	
09R1Cl3814	Removal of sand bag bund	4	05MAR10		1 67	3
09R1Cl3816	Construct temporary concrete block bund	8	10MAR10	10MAR10 30MAR10	1 67	
E.G. Valle	Aceivate a Gunstraki Approach Channel					
Phase 3	Sira habara kakana kaka da kata ka	N. C.	THE STATE OF THE S			
09R1Cl3902	Excavation of the Stream Bed	54	31MAR10	31MAR10 08JUN10	1 67	
09R1CI3904	Laying Granular Filter within Stream Bed	18	09JUN10 - 30JU	30JUN10	1 67	
09R1Cl3908	Open excavation for Approach Channel	69	02JUL10	20SEP10	1 67	
09R1Cl3910	Construction of Approach Channel	122	21SEP10	21SEP10 : 19FEB11	1 67	
09R1Cl3912	Construction of trash grill	12	14FEB11	26FEB11	1 67	
0CR1Cl3914	Removal of concrete bolck bund	9	28FEB11	05M	1 67	
	excavate a Construct Delegation Spanioer					
Phase 2	erronen en elektrikarian kara esta en elektrikarian interaktiona interaktiona interaktionale karationale karati		A 10 TO 10 T		· · · · · · · · · · · · · · · · · · ·	
06L1Cl3102	Excavation for de-aeration chamber	87	10JUL09	21OCT09	1 83	23 - 125 m 3 0 0 m 3/Hav - 124 byce
06L1Cl3104	Construction of de-aeration chamber	32	09JAN10	18FEB10	- 83	A Jours & week days invert drave walls 向 ave a succession of
	a cavalery box surrous administrati					<u> </u>
Phase 2	ocai alesa taran esperiaces esperiaces esperiación de esperiación de esperiación de esperiación de esperiación					
3CL1Cl3102	Mechanical excavation for Adit Tunnel	40	22OCT09	22OCT09 08DEC09	1 83	web/me @ udtm
3CL1Cl3104	Construction of Adit Tunnel	24	09DEC09	08JAN10	1 83	Sill Davis Books
3CL1Cl3106	Mechanical excavation breakthrough	12	22JUN10	22JUN10 06JUL10	1 206	
3CL1Cl3108	Construct collar between MT & AT	36	07JUL10	17AUG10	1 206	Mainvert, wall & roof
	Excavate to constitute Matrix organization tells					
Phase 2	CALLY CALLY THE PROPERTY OF TH	A COLUMN TO THE	Decada Garage Grand Control	A THE PROPERTY OF THE PROPERTY		
06L1Cl3122	Mechanical excavation for man access tunnel	53	02JUL09	01SEP09	1 170	mocking out access經過8m (@0.15m/dav
06L1Cl3124	Construction of man access tunnel	24	02SEP09	29SEP09	1 170	Sign Spays: 6 pours
	Aquianny Volks Pricing handoverny dienk					
09R1Cl3142	Finishing & reinstatement works; Portion C	48	07FEB11 02AP	02APR11	1 67	
09R1Cl3143	Pre-handover inspections and remedial works	48	O7MAR11 O5MA	05MAY11	1 67	
09R1Cl3144	Contractor serve notice for Works completion	2	06MAY11	12MA	2 480	
09R1Cl3146	SO issues completion certificate	21	13MAY11	02JUN11	2 480	
16R7Cl3142	Landscaping works at Portion C	120	06DEC10 05MA	05MAY11	1 68	
	Establishment Works at Portion C	365	06MAY11	04MAY12	2 83	
	Install flow measurement devices at Intake I-3	24	07FEB11 05MA	05MAR11	1 88	· · · · · · · · · · · · · · · · · · ·
3DL1Cl3143	Maintain & monitor flow monitoring	365	06MAR11 04MA	04MAR12	2 144	

| 13R 1; On completion of 30% soil natiling 0 28AUG08 2 1,488 ◆at intake I-3 13R 2; On completion of 60% soil natiling 0 25NOV08 2 1,399 ◆at intake I-3 13R 3; On completion of all soil nating works 0 12MAY09 2 1,231 ◆at intake I-3 13R 4; On completion of 10% piles by number 0 26MAY08 2 1,582 ◆at intake I-3 | 0 19FEB11 2 583 | channel 0 21JAN11 2 612 | G.L 0 24FEB09 2 1,308 | G.L 0 05SEP08 2 1,480 | 0 26MAR10 2 913
 |
 | 0 05MAY11 2 508 | 0 293EP09 2 1,091 | 0 23NOV09 2 1,036
 | 0 09FEB09 2 1,323 | n chamber 0 18FEB10 2 949 | 0 08.JAN11 2 625 | 0 21OCT09 2 1,069 Helmin C 1 |
 | C 0 17AUG10 2 769 | 0 08JAN10 2 990 | 31DEC09 2 998 | 0 : 28DEC09 2: 1,001 | 0 22DEC09 2 1,007 | 0 18DEC09 2 1,011 | 0 15DEC09 2 11.014
 | 11DEC09 2 1.018 | 0 210CT09: 2 1,069 | | ### Part Process Control of Contr | 109 2 1,018 109 2 1,014 109 2 1,011 109 2 1,001 100 2 1,001 100 2 1,001 100 2 1,001 100 2 1,001 100 2 1,001 100 2 1,009 100 2 1,036 100 2 1,036 100 2 1,036 100 2 1,036 11 2 1,031 11 2 1,159 12 1,159 13 2 1,159 14 2 1,159 15 2 1,159 15 2 1,159 15 2 1,159 15 2 1,159 15 2 1,159 15 2 1,159 15 2 1,159 15 2 1,159 15 2 1,159 16 2 1,159 17 2 1,159 18 2 1,159 19 <td< th=""><th></th><th>3CL1CI3A02 3CL1; On establishing tunnelling equipments 3CL1CI3A04 3cL 2; On completion of 12.5% perm. tunnel lining 3CL1CI3A08 3cL 4; On completion of 25% perm. tunnel lining 3CL1CI3A10 3cL 5; On completion of 50% perm. tunnel lining 3CL1CI3A11 3cL 5; On completion of 50% perm. tunnel lining 3CL1CI3A12 3cL 6; On completion of 50% perm. tunnel lining 3CL1CI3A14 3cL 7; On completion of 50% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of 62.5% of excavation at G.L 3CL 1CI3A18 3cL 9c 9c 3cm on forex shaft 3CL 1CI3A18 3cL 9c 3cm on for</th></td<> | | 3CL1CI3A02 3CL1; On establishing tunnelling equipments 3CL1CI3A04 3cL 2; On completion of 12.5% perm. tunnel lining 3CL1CI3A08 3cL 4; On completion of 25% perm. tunnel lining 3CL1CI3A10 3cL 5; On completion of 50% perm. tunnel lining 3CL1CI3A11 3cL 5; On completion of 50% perm. tunnel lining 3CL1CI3A12 3cL 6; On completion of 50% perm. tunnel lining 3CL1CI3A14 3cL 7; On completion of 50% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of 62.5% perm. tunnel lining 3CL1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of forex shaft 3CL 1CI3A18 3cL 9; On completion of 62.5% of excavation at G.L 3CL 1CI3A18 3cL 9c 9c 3cm on forex shaft 3CL 1CI3A18 3cL 9c 3cm on for |
|---|---|---|---|--

--
---|--|---|--
--|---|--|--|---
--|---|--|----------------------|---|---
---|---|--|--|--|---|--------------------
--|
| | 0 05/MAY11 2 508 | 2 0 19FEB11 2 583 | Columbia Columbia | G.L 0 24FEB09 2 1,308 G.L 0 12MAY09 2 1,159 nef 0 23JUL09 2 1,159 nef 0 2JJAN11 2 674 0 19FEB11 2 583 0 19FEB11 2 508 0 19FEB11 2 508 | Columbia Columbia | G.L 0 26MAR10 2 913 Pat Intake I-3 Pat Intake I-3 G.L 0 24FEB09 2 1,1308 Pat Intake I-3 Pat Intake I-3 <td< td=""><td> Channel and associated decking at Intake I-3 Channel at Intake I-3 Chann</td><td> C O O O O O O O O O</td><td>C 0 29SEP09 2 1,091 Punder this Cost C 0 0 26MAY11 2 508 G.L 0 26MAR10 2 913 Punder this Cost G.L 0 26MAR10 2 913 Punder this Cost G.L 0 26FEB09 2 1,231 Pat Intake I-3 Pat Intake I-3 Pat Intake I-3 G.L 0 23JUL09 2 1,159 Pat Intake I-3 Pat Intake I-3</td><td>C 0 23NOV09 2 1,034 C 0 28SEP09 2 1,091 C 0 28SEP09 2 1,091 C 0 28MAPTI 2 913 GL 0 28FEB09 2 1,308 GL 0 24FEB09 2 1,308 GL 0 23JUL09 2 1,139 mel 0 22JUL09 2 1,139 0 21JANTI 2 674 0 21JANTI 2 583 0 19FEB11 2 583 0 19FEB11 2 583</td><td>0 0 09FEB09 2 1,332 ◆at Intake I-3 <</td><td>0 18FEB10 2 943 Pat Intake I.3 Pat Intake I.3 Pat Intake I.3 0 0 23NDV09 2 1,323 1,323 1,323 Pat Intake I.3 Pat Intake I.3 Pat Intake I.3 Pat Intake I.3 Punder this Cost C 0 28SED09 2 1,333 Pat Intake I.3 Pat Intake</td><td>0 0</td><td> 0 21OCT09 2 11,069 Colored G.L. except for Adit Tunnel at Intake I-3 O O OSNAVT1 2 E25 O O OSSNAVT1 2 E35 O OSSNAVT1 2 E35 O O OSSNAVT1 2 O O OSSNAVT1 D O OSSNAVT1 O O O OSSNAVT1 O O O O OSSNAVT1 O O O O O OSSNAVT1 O O O O O O O O O </td><td> 0 21/OCT09 2 1,069 </td><td>C 0 17ALG10 2 769 0 0 0 0 0 0 0 0 0 4 belowe G.L. except for Adit Tunnel at Intake I-3 4 under this Cost Centre 0 0 0 0 0 0 4 belowe G.L. except for Adit Tunnel at Intake I-3 4 at Intake I-3 <th< td=""><td> C</td><td> 1</td><td> 1</td><td> 10 10 10 10 10 10 10 10</td><td> 10 18DEC09 2 1,017 </td><td> 150EC09 150EC09 2 1,014 </td><td> 10 10 10 10 10 10 10 10</td><td> 10</td><td>Wunder this Dost C</td><td></td><td></td><td>indices i centralité de partir</td></th<></td></td<> | Channel and associated decking at Intake I-3 Channel at Intake I-3 Chann | C O O O O O O O O O | C 0 29SEP09 2 1,091 Punder this Cost C 0 0 26MAY11 2 508 G.L 0 26MAR10 2 913 Punder this Cost G.L 0 26MAR10 2 913 Punder this Cost G.L 0 26FEB09 2 1,231 Pat Intake I-3 Pat Intake I-3 Pat Intake I-3 G.L 0 23JUL09 2 1,159 Pat Intake I-3 | C 0 23NOV09 2 1,034 C 0 28SEP09 2 1,091 C 0 28SEP09 2 1,091 C 0 28MAPTI 2 913 GL 0 28FEB09 2 1,308 GL 0 24FEB09 2 1,308 GL 0 23JUL09 2 1,139 mel 0 22JUL09 2 1,139 0 21JANTI 2 674 0 21JANTI 2 583 0 19FEB11 2 583 0 19FEB11 2 583 | 0 0 09FEB09 2 1,332 ◆at Intake I-3 < | 0 18FEB10 2 943 Pat Intake I.3 Pat Intake I.3 Pat Intake I.3 0 0 23NDV09 2 1,323 1,323 1,323 Pat Intake I.3 Pat Intake I.3 Pat Intake I.3 Pat Intake I.3 Punder this Cost C 0 28SED09 2 1,333 Pat Intake I.3 Pat Intake | 0 | 0 21OCT09 2 11,069 Colored G.L. except for Adit Tunnel at Intake I-3 O O OSNAVT1 2 E25 O O OSSNAVT1 2 E35 O OSSNAVT1 2 E35 O O OSSNAVT1 2 O O OSSNAVT1 D O OSSNAVT1 O O O OSSNAVT1 O O O O OSSNAVT1 O O O O O OSSNAVT1 O O O O O O O O O | 0 21/OCT09 2 1,069 | C 0 17ALG10 2 769 0 0 0 0 0 0 0 0 0 4 belowe G.L. except for Adit Tunnel at Intake I-3 4 under this Cost Centre 0 0 0 0 0 0 4 belowe G.L. except for Adit Tunnel at Intake I-3 4 at Intake I-3 <th< td=""><td> C</td><td> 1</td><td> 1</td><td> 10 10 10 10 10 10 10 10</td><td> 10 18DEC09 2 1,017 </td><td> 150EC09 150EC09 2 1,014 </td><td> 10 10 10 10 10 10 10 10</td><td> 10</td><td>Wunder this Dost C</td><td></td><td></td><td>indices i centralité de partir</td></th<> | C | 1 | 1 | 10 10 10 10 10 10 10 10 | 10 18DEC09 2 1,017 | 150EC09 150EC09 2 1,014 | 10 10 10 10 10 10 10 10 | 10 | Wunder this Dost C | | | indices i centralité de partir |
| * under this | ▼ | 0 19FER1 2 | 1.L 0 12MAY09 2 1,231 | 1.L 0 24FEB09 2 1,308 1.L 0 12MAY09 2 1,231 0 23JUL09 2 1,159 1 0 20NOV10 2 674 0 21JAN11 2 612 0 19FER11 2 529 | 1.L 0 0 05SEP08 2 1.480
 | 1.L 0 0 26MAR10 2 913
1.L 0 0 24FEB09 2 1,231
1.L 0 0 24FEB09 2 1,231
0 0 23JUL09 2 1,531
el 0 22JAN11 2 612
0 21JAN11 2 612
 | 0 26MAR10 2 913 | 0 05MAY11 2 508 L 0 0 26MAR10 2 913 L 0 0 05SEP08 2 1,480 L 0 0 24FEB09 2 1,308 0 0 23JUL09 2 1,159 0 0 20NOV10 2 674 0 0 21JAN11 2 612 0 0 19FER11 2 503 | 0 29SEP09 2 1.091
 | 0 23NOV09 2 1,036 Part Intake I-3 Part Intake I-3 Part Intake I-3 Punder this Cost 0 0 0 05MAY11 2 508 4 | 0 0 0 0 0 0 23NOV09 2 1,323 ◆at Intake I-3 ◆orlation intake I-3 ◆orlationer at Intake I-3 | 0 18FEB10 2 943 Pat Intake I-3 Chamber at Intake I-3 Pat Intake | 0 | 0 0 0 0 0 0 0 0 0 0 | 0 210CT09 2 1,059 2 | C 0 17AUG10 2 759 0 21OCT09 2 1,069 Purder this Cost Centre 0 0 21OCT09 2 1,069 Purder this Cost Centre 0
 0 | 1 | 3 DEC09 2 999 | 1 | 1 | 18DECO9 2 1,001 2 1 | 150EC09 150EC09 2 1,014 | 11 12 12 13 14 15 15 15 15 15 15 15 | 10 110EC09 2 1,0104 2 1,0104 3 4 4 1 1 1 1 1 1 1 1 | at Intake I-3
 | N CI | 0 | in of all works under this CC |
| 0 21JAN11 2 612 channel and associated deliving at Intake I-3 value Intake I-3 0 19FEB11 2 583 4at Intake I-3 4at Intake I-3 0 0 05MAY11 2 508 4at Intake I-3 | channel 0 21JAN11 2 612 | | 0 12MAY09 2 1,231 | 0 24FEB09 2 1,308 | 0 05SEP08 2 1,480
 | 0 26MAR10 2 913 0 05SEP08 2 1,480 0 24FEB09 2 1,308 0 12MAV09 2 1,231 0 23JUL09 2 1,159
 | 0 26MAR10 2 913 | 0 05MAY11 2 508 | 0 29SEP09 2 1.091
 | 0 23NOV09 2 1,036 0 29SEP09 2 1,091 Padit at Intake I-3 Padit at Intake I-3 Punder this Cost 0 26MAPTI 2 913 Punder this Cost Padit at Intake I-3 Punder this Cost L 0 24FEB09 2 1,231 Padit Intake I-3 Padit Intake Intake Intake Intake Intake Intake Intake Intake Int | 0 09FEBO9 2 1,338 ◆at Intake I-3 ◆adit at Intake I-3 ◆adit at Intake I-3 0 23NOV09 2 1,091 ◆adit at Intake I-3 ◆adit at Intake I-3 ◆under this Cost 0 05MAY11 2 508 +at Intake I-3 ◆at Intake I-3 ◆under this Cost L 0 24FEB09 2 1,231 ◆at Intake I-3 ◆at Intake I-3 ◆at Intake I-3 L 0 24FEB09 2 1,231 ◆at Intake I-3 ◆at Intake I-3 ◆at Intake I-3 | 0 | 0 | 0 21/OCT09 2 i j,069 CGNOV10 2 i j,069 Belowe G.L. escept for Adit Tunnel at Intake I-3 Cotamble Intake I-3 Pelow G.L. escept for Adit Tunnel at Int | 0 21OCT09 2 1,069 0 05NOV10 2 625 belowe G.L. except for Adit Tunnel at Intake I-3 Pat Intake I- | C
 0 17AuG10 2 769 Actin Tunnel at Inhake 1.3 Punder this Cost Centre 0 21OCT09 2 ii.069 2 ii.069 2 ii.069 4 below G.L. escept for Adit Tunnel at Inhake 1.3 4 chamber at Inhake 1.3 <td> 1</td> <td> 1</td> <td> 1</td> <td> 0 22DEC09 2 1,007 </td> <td> 1 10 10 10 10 10 10 10</td> <td> Section 15DE-C09 2 1,014 </td> <td> 10</td> <td> 10</td> <td>י מו ווומוע ו-ט</td> <td>2</td> <td>0</td> <td>on of 50% of approach channel</td> | 1 | 1 | 1 | 0 22DEC09 2 1,007 | 1 10 10 10 10 10 10 10 | Section 15DE-C09 2 1,014 | 10 | 10 | י מו ווומוע ו-ט
 | 2 | 0 | on of 50% of approach channel |
| nnel 0 20NOV10 2 674 | oproach channel 0 20NOV10 2 674 channel 0 21JAN11 2 612 | 0 20NOV10 2 674 | 12MAY09 2 1,231 | G.L 0 24FEB09 2 1,308 | G.L 0 05SEP08 2 1,480 | G.L 0 26MAR10 2 913 ◆at Intake I-3 G.L 0 05SEP08 2 1480 ◆at Intake I-3 G.L 0 24FEB09 2 1;308 ◆at Intake I-3 G.L 0 12MAY09 2 1;231 ◆at Intake I-3 | L 0 28MAR10 2 913 ◆at Intake I-3 ◆at Intake I-3 ◆at Intake I-3 ◆at Intake I-3 L 0 24FEB09 2 1,308 ◆at Intake I-3 ◆at Intake I-3 ◆at Intake I-3 | 0 OSMANY11 2 508 Cunder this Cost L 0 26MAR10 2 913 Cunder this Cost Cunder this C | 0 29SEP09 2 1,091 0 05MAY11 2 508 L 0 26MAR10 2 1,480 L 0 24FEB09 2 1,231 L 0 12MAY09 2 1,231 | 0 23NOV09 2 1,036 0 29SEP09 2 1,091 0 0 0 0 0 26MAP10 2 913 0 0 05SEP08 2 1,308 L 0 24FEB09 2 1,308 L 0 12MAY09 2 1,231 | 0 09FEBO9 2 1,323 ◆at Intake I-3 ◆adit at Intake I-3 0 23NOV09 2 1,091 ◆adit at Intake I-3 ◆adit at Intake I-3 ◆under this Cost 0 05NAY11 2 508 4 | 0 18FEB10 2 949 Pat Intake I-3 Pat Intake | 0 0 0 0 0 0 0 0 0 0 | 0 21OCT09 2 i nose Pelowe G.L. escept for Adit Tunnel at Intake I-3 Pelowe G.L. escept for Adit Tunnel at Intake I-3 Pat Intake I-3 | 0 21OCT09 2 1,089 Belowe G.I. escept for Adif Tunnel at Intake I-3 Achamber at Intak | C 0 17AuG10 2 759 Purple at Inhake I-3 Purple at Inhake I- | C OBJANTO 2 990 Patit Tunnel at Intake 3 Patit Tunnel at Int | 1 | 1 | 0 22DEC09 2 1,007 4 Adit Turnel at Intake 1-3 1,007 4 Adit Turnel at Intake 1-3 4 Adit Turnel at Intake 1-3 | 1 10 1 10 10 10 10 10 | 150EC09 2 i i j j j j j j j j j j j j j j j j j | 1 | 10 | , d | 8 | 0 | on of excavation at G.L. |
| nnel 0 23JUL09 2 1159 Pequannel Pequannel Pequannel Intake I-3 Pequannel Pequannel Intake I-3 Pequannel Intake I-3 Pequannel Intake I-3 Pequannel Intake I-3 Pepulation Intake I-3 Pepulation Intake I-3 Pepulation Pepulation Intake I-3 Pepulation Pepulation Intake I-3 Pepulation Pepulation Intake I-3 Pepulation Pepulation Pepulation Intake I-3 Pepulation | oproach channel 0 23JUL09 2 1,159 oproach channel 0 20NOV10 2 674 channel 0 21JAN11 2 612 | 0 23JUL09 2 1,159 4at G.L. at Intake I-3 0 20NOV10 2 674 | | G.L 0 24FEB09 2 1,308 | G.L 0 05SEP08 2 1,480
 | G.L 0 26MAR10 2 913 Pat Intake I-3 G.L 0 05SEP08 2 1,480 Pat Intake I-3 G.L 0 24FEB09 2 1,308 Pat Intake I-3
 | Cost | 0 05/MAY11 2 508 L 0 26MAR10 2 913 L 0 24FEB09 2 11,308 | 0 29SEP09 2 1,091 0 05MAY11 2 508 L 0 26MAR10 2 913 L 0 05SEP08 2 1,480 L 0 24FEB09 2 1,308 | 0 23NOV09 2 1,036 0 29SEP09 2 1,091 0 05MAY11 2 508 L 0 26MAR10 2 1,480 L 0 24FEB09 2 1,480 L 0 24FEB09 2 1,308 | 0 09FEB09 2 1,323 ◆at Intake I-3 ◆adit at Intake I-3 0 23NOV09
 2 1,031 ◆adit at Intake I-3 ◆adit at Intake I-3 0 25SEP09 2 1,091 ◆adit at Intake I-3 ◆adit at Intake I-3 ◆under this Cost L 0 28MARTIO 2 91,309 ◆at Intake I-3 ◆at Intake I-3 ◆at Intake I-3 | 0 18FEB10 2 949 Pat Intake I-3 Pat Intake Intake I-3 Pat Intake | 0 08JAN11 2 625 00 08JAN11 2 625 00 00 00 00 00 00 00 | 0 21OCT09 2 i1,089 belowe G.L. escept for Adit Tunnel at Intake I-3 below G.L. escept for Adit Tunnel at Intake I-3 thrake I-3 at Intake I-3 | 0 210CT09 2 1,069 0 05NOV10 2 689 0 0 0 0 0 0 0 0 0 | C 0 17AUG10 2 789 Purple Intrake I-3 Purple Intr | 1 | 1 | 1 | 0 220EC09 2 1,007
 | 9 0 18DEC09 2 1,001 in 0 22DEC00 2 1,007 in 0 28DEC09 2 1,001 in 0 0 8DEC09 3 1,001 in 0 0 0 0 0 0 8DEC09 3 1,001 in 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 | 150EC09 2 1,014 | 1 | 1 1 1 2 1 1 1 1 2 1 1 | at Intake | 0 | 0 | n of 75% of excavation at G.L
 |
| 150EC09 2 1,009 2 1,001 4,000 2 1,001 4,000 2 1,001 4,000 2 1,001 | 0 2100709 2 1,099 0 1100500 2 1,014 0 150500 0 15 | 0 2100T09 2 1,009 0 1,000 0 1 | 0 | 0 210CT09 2 1,069 0 110EC09 2 1,001 0 22DEC09 2 1,001 0 22DEC09 2 1,001 0 22DEC09 2 1,001 0 22DEC09 2 1,001 0 310EC09 2 1,001 0 05AN11 2 625 0 05AN11 2 625 0 05AN11 2 625 0 05AN11 2 625 0 05AN11 2 1,001 0 05AN11 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 | 210CT09 2 1,069 2 1,069 2 1,069 2 1,018 3 4 4 1 1 1 1 1 1 1 1
 | 210CT09 2 1,069
 | 210CT09 2 1,069 | 210CT09 2 1,069 15DEC09 2 1,014 15DEC09 2 1,014 18DEC09 2 1,011 22DEC09 2 1,001 22DEC09 2 1,069 2 1,069 2 1,069 2 1,069 2 1,323 23NOV09 2 1,388 | 110 210 2 1,069 2 1,069 2 1,014 150 2 1,014 150 2 1,014 150 2 1,011 150 2 1,011 150 2 1,011 150 2 1,011 170 17 | 110EC09 2 1,069 4 euipment 150EC09 2 1,014 4 euipment 150EC09 2 1,014 4 euipment 180EC09 2 1,001 220EC09 2 1,001 280EC09 2 1,001 4 euipment 280EC09 2 1,001 280EC09 2 1,001 4 euipment 5 euipment 6 euipment | 210CT09 2 1,069 15DEC09 2 1,014 15DEC09 2 1,014 15DEC09 2 1,011 22DEC09 2 1,001 28DEC09 2 1,001 31DEC09 2 998 31DEC09 2 998 31DEC09 2 998 4Adit 08JAN10 2 990 17AUG10 2 797 17AUG10 2 797 17AUG10 2 889 05NOV10 2 689
 | 210CT09 2 1,069 11DEC09 2 1,014 15DEC09 2 1,011 22DEC09 2 1,001 28DEC09 3 1,00 | 210CT09 2 1,069 Padit Tunnel 15DEC09 2 1,014 Padit Tunnel 15DEC09 2 1,014 Padit Tunnel 22DEC09 2 1,001 28DEC09 2 1,001 31DEC09 2 998 Padit Tunnel Pad | 21OCT09 2 1,069 11DEC09 2 1,014 15DEC09 2 1,014 18DEC09 2 1,007 22DEC09 2 1,007 28DEC09 2 1,007 31DEC09 2 990 08JAN10 2 990 20JUL10 2 797 | 210CT09 2 1,069 Padit Tunnel 15DEC09 2 1,014 Padit Tunnel 18DEC09 2 1,014 Padit Tunnel 22DEC09 2 1,007 Padit Tunnel 23DEC09 2 1,007 Padit Tunnel 31DEC09 2 990 Padit Tunnel 220JUL10 2 990 Padit Tunnel 220JUL10 2 20JUL10 2 207 | 210CT09 2 1,069 11DEC09 2 1,018 15DEC09 2 1,014 18DEC09 2 1,007 22DEC09 2 1,007 22DEC09 2 1,007 31DEC09 2 1,007 31DEC09 2 998 | 210CT09 2 1,069 11DEC09 2 1,018 15DEC09 2 1,014 18DEC09 2 1,007 22DEC09 2 1,007 28DEC09 2 1,007 28DEC09 2 1,007 | 210CT09 | 210CT09 2 1,069 11DEC09 2 1,018 15DEC09 2 1,014 18DEC09 2 1,014 | 21OCT09 2 1,069
 | 210CT09 2 1,069 Peulpment for tunnelling at Intake | 21OCT09 2 1 069 | TOTAL STATE OF THE PROPERTY OF | | 2224/2322/2027/2027/22/24/25/25/25/25/25/25/25/25/25/25/25/25/25/ | | には、自己の名の形式は自己の一方式を |
 |

M2*40*4m2	12 18AUG10 31AUG10 1 8	10R1D00704 Drive temp. sheet piles along footpath
	12 04AUG10 17AUG10 1 8	10H1DO0702 Form temp. working platorm
		Constituto cascade y Upiter Par Box Conver
810	24 07JUL10 03AUG10 1 8	3AL1DO0606 Construct portal head wall
Fror TBM Launching Chamber	12 22JUN10 06JUL10 1 8	3AL1DO0604 Construct permanent lining for CH5100-5085
Eningliang gahtry crane	30 15MAY10 21JUN10 1 8	
313	12 18DEC10 04JAN11 1 8	
	48 04AUG10 29SEP10 1 74	10R1DO0604 Construct tapered open channel
86	24 07JUL10 03AUG10 1 8	10R1DO0802 Excavation/formation for tapered open channel
		construct Parel Read & Tussociated Statutess
6.50	6 01MAR11 07MAR11 1 39	10R1DO0528 Reinstate existing outfall "W"
	28FEB11 1	10R1DO0526 Construct open channel at 2.3 mPD
	24 14JAN11 14FEB11 1 39	10R1DO0524 Construct channel toe below 2.3mPD
	24 30DEC10 27JAN11 1 39	10R1DO0522 Excavate for open channel
	40 11NOV10 29DEC10 1 39	10R1D00520 Construt wall & roof of box culvert; 2 cells
Chocete 160m3	20 19OCT10 10NOV10 1 39	10R1D00518 Construct base slabs of box culvert; 2 cells
Comments of the state of the st	25AUG10 18OCT10 1	10R1D00516 Excavate for box-culvert; 2 cells
	40 TIMAY10 28JUN10 1 39	10R1DO0515 Install 273mm dia temp, pile for nine modina
/II/Concete 160m3	16APR10 10MAY10 1	10H1DU00512 Construct base slabs of box culvert; 2 cells
(KEW) SOI 2900m3	19FEB10	10R1DO0510 Excavate for box-culvert; 2 cells
Resignation 2 cells; 105 rlos.	48 18DEC09 18FEB10 1 39	
E	24 20NOV09 17DEC09 1 39	10R1DO0506 Excavate & form pipe roofing platform @+2.3mPD
	36 08OCT09 19NOV09 1 39	10R1DO0504 Divert exist. outfall "W" under CPR arch bridge
	0 08OCT09 2 47	10R1D00502 Site possession of Portion E-650d of DOC
		Constanct tower Partition Sulvert & Ocen Channel
	12 11JUN10 25JUN10 1 40	10R1DO0424 Commission of Spiral Ramp
	24 13MAY10 10JUN10 1 40	10R1D00422 Construct vehicular access bet. tunnel & s. ramp
	27NOV09 27APR10 1	10H1D00416 Construct spiral ramp; +4.5 to +24mPD at O-1
		_
	16 24OCT09 12NOV09 1 40	-
	8 15OCT09 23OCT09 1 40	10R1DO0410 Construct base for vehicular access
sheet pile roofing & lagging ~180m2@asoil 640m3	48 18AUG09 14OCT09 1 40	10R1DO0408 Excavation for vehicular access underneath CPR
740th3 soil & 4000m3 rock翻翻翻回回口口口口口口口口口口口口口口口口口口口口口口口口口口口口口口口口口	120 21MAR09 17AUG09 1 40	10R1DO0404 Mechanical excavation for spiral ramp
340 nos. +13m lono	12 07MAR09 20MAR09 1 40	10R1DO0402 Install 273mm dia. temp. pipe piles; 40 nos.
7. B. B. D. D. D. B.	Dur Starf Finish 15 Float	
STATE OF THE PARTY	Early Cal Total	To the second se
		は、日本の大学の一個などのでは、日本の大学の大学の日本の大学の大学の大学の大学の大学の大学の大学の大学の大学の大学の大学の大学の大学の

42
ō
40
ĕ
뚮
-

	Start Finish 10 Float	11E MANNELLA SIBONDI JERIKANIJA YSONDI JERIKANI MATANIKANI PARABATANI MANJA SIONDI KASANI MANJA KASI 8 8 MOLI 12 BUSI 17 BUSI KASANI KASANI MASANDI KASANI KANDANI KANDANI KASANI KANDANI KANDANI KANDANI KANDANI K
10R1DO0706 Excavate for box culvert (upper part)	_	Emiliano de la companya de la compan
10R1DO0708 Construct box-culvert (upper part)	15OCT10 04JAN11 1	Emission concrete 1830m3
10R1DO0710 Excavate for cascade construction	05JAN11	##Soi 840m3, rock 600m3
10R1DO0712 Construct cascade	48 19FB11 16APR11 1 8	Email:concrete 950m3
10R1D00714 Construct retaining wall, baffle, railing etc.	48 19FEB11 16APR11 1 33	
Seabethrotestion.Works		
10R1DO0804 Excavate & formation for 100m*16m slab	72 11MAY10 05AUG10 1 93	INERNOS Soil 4000m3
10R1D00806 Construct concrete apron with pre-cast RC slabs	26MAY10 19AUG10 1	国际管理 1600°0.5m3
10R1DO0808 Installtion of precast stepped blocks	144 06AUG10 27JAN11 1 93	pre-cast panel 2340m2, granular filter 700m3Faster 2346mg 300mm granular fill & geotextile
10R1DO0810 Removal of platform & formation	12 08MAR11 21MAR11 1 39	128
10R1D00812 Install remain. Concrete apron for rem. Area	12 22MAR11 04APR11: 1 39	163
14R5DO0802 Removal of sea wall armour	72 26APR10 22JUL10 1 93	[Nation 3640m3
RepainingsWorks From 19th and over		
10R1D00904 Finishing & reinstatement works; Portion D	48 19MAR11 19MAY11 1 33	
10R1DO0906 Pre-handover inspections and remedial works	48 18APR11 17JUN11 1 33	
10R1D00908 Contractor serve notice for Works completion	7 18JUN11 24JUN11 2 437	
10R1D00910 SO issues completion certificate	21 25JUN11 15JUL11 2 437	£32
i 16R7DO0902 Landscaping works at Portion D	120 19JAN11 17JUN11 1 33	
16R7D00904 Establishment Works at Portion D	365 18JUN11 16JUN12 2 40	
3DL1D00902 Install flow measurement devices at Outfall O-1	24 18APR11 19MAY11 1 29	瑟
37L1D00904 Maintain & monitor flow monitoring	365 20MAY11 18MAY12 2 69	
Scheddleiofalliesionesablicosi Centento author		
110R1DO1002 10R 1; On completion of 20% excavation works	0 09JUL08 2 1,538	♦Outill 6-1
10R1DO1004 10R 2; On completion of 40% excavation works		♦Outrail 0-1
10R1DO1006 10R 3; On completion of 60% excavation works	08NOV08 2	♦ Optrall Q-1
10R1DO1008 10R 4; On completion of 80% excavation works	14OCT09 2 1,	Onitail O-i
10R1DO1010 10R 5; On completion all excavation works	18FEB11	eat Outfall 0-1
10R1DO1014 10R 7: On completion of social ramp to ±16mPD	1 6	tar Cutral O-1
10R1DO1016 10R 8; On completion of spiral access ramp	25JUN10 2	◆at Outfall O-1
10R1DO1018 10R 9; On completion box-culvert & open channel	0 07MAR11 2 567	◆and open channel underneath CPR
10R1DO1020 10R 10; On completion of seabed protection wks	0 04APR11 2 539	Protection works at Outfall O-1
10R1DO1022 10R 11; On completion of all works under this CC	0 17JUN11 2 465	&under this Cost Centre
September of the statement of the statem		
14R5DO1102 14R 1; On complet. of remove exist. rock armour	8	♦armour al Outfall O-1
	20JUN08 2	In the second of
14R5DO1106 14R 3; On completion all soiling works	0 13AUG08 2 1,503	◆nalling at Outfall O-1

4
ö
54
Sheet

SOLVEN STANDARD STAND	◆pipe jacking method at Portion G	Dipe jacking method at Portion G	Spipe jacking method at Portion G	Spipe facking method at Portion G	Sunder this Cost Centre
A NATIONAL STATES					
1000					
NO S					
1000					
7 (2) (3)			;		
SON 0					
2008 Maria 12131415					
M N N S S S S S					
otal loat	664	929	647	636	480
	7	α	~	2	5
arly nish	30NOV10	08DEC10	7DEC10	EC10	UN11
Early Finisi	30NO	080	17DEC	28DEC	02JUN
Start					
Ong Early Dur Stan	0		0	0	0
				-	
	ging	sing .	king		ils CC
, E	pipejac	pipejacl	pipejacl	acking	ınder th
Activa Sector	52% of	50% of	75% of	all pipej	all wks t
1	tion of	tion of	ition of	tion of	tion of
	comple	comple	comple	comple	comple
	H 2; On	я 3; О	R 4; On	R 5; On	R 6; On
	504 15	506 15	308 15	310 15	512 15
e	15H6GG0504 15R 2; On completion of 25% of pipejacking	5R6GG0506 15R 3; On completion of 50% of pipejacking	5R6GG0508 15R 4; On completion of 75% of pipejacking	15R6GG0510 15R 5; On completion of all pipejacking	15R6GG0512 15R 6; On completion of all wks under this CC
ing Tagan	ក	2	15	15	151



Appendix D

Implementation Status of Environmental Mitigation Measures

IMPLEMENTATION SCHEDULE July 2008

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status
Air Q	<u>uality</u>				
3.6.1	As mentioned in Section 3.5, exceedances of 1-hour and 24-hour average TSP guideline levels have been predicted at most of the ASRs. Hence, mitigation measures are considered necessary in order to suppress the potential dust impact. The dust suppression measures set out in the <i>Air Pollution Control (Construction Dust) Regulation</i> , in fact, are more extensive. Therefore, it is expected that with watering the	DSD's Contractor	Construction Work Sites	Air Pollution Control (Construction Dust) Regulation	N/A
	construction site every four times daily together with strict implementation of dust suppression measures as stipulated in the <i>Air Pollution Control (Construction Dust) Regulation</i> , the dust level is expected to be reduced by over 75%.				N/A
	General				
	To further ensure compliance with the guideline and AQO limit at the ASRs at all time, it is recommended to implement the <i>Air Pollution Control (Construction Dust) Regulation</i> and include good site practice in the contract clauses to minimize cumulative dust impact. In addition, a comprehensive dust monitoring and audit programme is recommended to ensure proper implementation of the identified mitigation measures. Details of the monitoring and audit requirements are provided in a separate EM&A Manual.				
	• effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building or if a canopy is provided at the first floor level, from the first floor level, up to the highest level of the scaffolding where a scaffolding is erected around the perimeter of a building under construction;				N/A
	dump truck for material transport should be totally enclosed by impervious sheeting;				\checkmark
	 any excavated dusty materials or stockpile of dusty materials should be covered entirely by impervious sheeting or sprayed with water so as to maintain the entire surface wet, and recovered or backfilled or reinstated within 24 hours of the excavation or unloading; 				✓
	 stockpile of dusty materials should not extend beyond the pedestrian barriers, fencing or traffic cones; 				√
	 dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; 				√

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status	
3.6.1	• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;	DSD's Contractor	Construction Work Sites	Air Pollution Control (Construction Dust) Regulation	✓	
	 where a site boundary adjoins a road, street or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length except for a site entrance or exit; 				✓	
	• every main haul road should be scaled with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet;				✓	
	• the portion of road leading only to a construction site that is within 30m of a designated vehicle entrance or exit should be kept clear of dusty materials;				✓	
	stockpile of dusty materials should be either covered entirely by impervious sheeting, placed in an area sheltered on the top and the 3 sides; or sprayed with water so as to maintain the entire surface wet;				✓	
	all dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty material wet;				✓	
	vehicle speed should be limited to 10 kph except on completed access roads;				✓	
	• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites;				✓	
	the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle; and					✓
	• the working area of excavation should be sprayed with water immediately before, during and immediately after the operations so as to maintain the entire surface wet.				✓	
Noise						
4.6.1	During Construction Appropriate mitigation measures such as the use of quiet equipment and movable barriers will be developed to ensure that noise can be reduced to acceptable levels without causing programme delays	DSD's Contractor	Construction Work Sites	PN 2/93 Noise from Construction Activities & EIAO	N/A	
	Good Site Practice Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures should be followed during construction:					
	 only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction works; 				✓	
	 machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; 				✓	

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status	
4.6.1	• plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs;	DSD's Contractor	Construction Work	Air Pollution Control (Construction Dust)	✓	
	mobile plant should be sited as far away from NSRs as possible; and		Sites	Regulation	\checkmark	
	• material stockpiles and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities.				✓	
	 For Drill and Blast Works Charge mass per delay should be decreased by minimising the number of blastholes firing on each delay. 				N/A	
	Smaller blasthole patterns and longer delays should be used between dependent charges.				N/A	
	Times of blasting should be established to suit the situation and firing blasts when neighbours are busy with their daily tasks (and at a regular time such as lunch time).					N/A
	For the tunnel excavation, it is anticipated that beyond the initial length (say within 30m), excavation will be carried out well within the tunnel and door should be provided to further minimize the noise nuisance to the nearby receivers.				N/A	
4.6.2	During Operation	DSD's Contractor	Project Area	NCO & EIAO		
	Good site practice and noise management can significantly reduce the impact of maintenance activities on nearby NSRs. The following package of measures should be followed during construction	Contractor				
	only well-maintained plant should be operated on-site;				N/A	
	machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; and				N/A	
	• plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs.				N/A	
	Quality					
5.9.1	During Construction	DSD's Contractor	Construction Work Sites	Practice Note for Professional Persons with	√	
	Mitigation measures and a spill control and response plan have been prepared for works at the intakes and work sites.			regard to site drainage (ProPECC PN 1/94) and WQO		
	Precautions to be taken at any time of year when rainstorms are likely:				✓	
	 Temporarily exposed surfaces should be covered e.g. by tarpaulin. Temporary access roads should be protected by crushed stone or gravel. 	-			✓	
	Trenches should be dug and backfilled in short sections. Measures should be taken to minimize the ingress of rainwater into trenches.	-			✓	
	Actions to be taken when a rainstorm is imminent or forecast: • Silt removal facilities, should be checked to ensure that they can function properly.				✓	

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status			
.9.1	 Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric. 	DSD's Contractor	Construction Work Sites	WQO	✓			
	All temporary covers to slopes and stockpiles should be secured.				✓			
	 Actions to be taken during or after rainstorms: Silt removal facilities should be checked and maintained to ensure satisfactory working conditions. 				✓			
	Spill Control and Response Plan							
	1 Prevention and Precaution Measures							
	General PrecautionsNo discharge of silty water into watercourses.				✓			
	 All materials to be used during construction and operation shall be identified and their hazard potential evaluated. 				✓			
	 Maintenance of vehicles and equipment involving activities with potential for leakage and spillage shall only be undertaken with the areas appropriately equipped to control these discharges. 				✓			
	 Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials. 				✓			
	 Any construction plant which causes pollution to catchwaters or water gathering ground due to leakage of oil or fuel shall be removed off-site immediately. 					✓		
	 Suitable containers shall be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport 					✓		
	 Chemical waste containers shall be suitably labelled to notify and warn the personnel who are handling the wastes to avoid accidents. 					✓		
	• Storage areas shall be selected at safe locations on site and adequate space shall be allocated to the storage area.					✓		
	• Prevent obstructions and tripping hazards.				✓			
	Storage PrecautionsAll chemical storage containers shall be correctly labelled.							✓
	Solid and impermeable enclosure walls or storage shelves shall be used.							
	Only compatible chemical wastes shall be stored in the same storage area.						✓	
	• The storage areas shall be inspected to detect any leakages or defective containers on a regular basis.							\checkmark
	• The storage areas shall be inspected to detect any leakages or defective containers on a regular basis.						✓	
	• Suitable notices warning of hazards, emergency response plans, telephone numbers etc shall be posted around the site, including storage areas.						✓	
	Large and heavy containers shall be stored at ground level.				✓			

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status
	Chemical waste containers shall be stored below eye level.				✓
5.9.1	Adequate space for handling of the containers shall be provided	DSD's	Construction	WQO	√
	• Spill response kits shall be located adjacent/near to the storage areas.	Contractor	Work Sites		\checkmark
	A log of chemical wastes shall be maintained.				✓
	Incompatible chemicals shall be stored separately.				✓
	2 Responses/Action Plan				
	All Workers shall be made aware of emergency telephone numbers and the location of all relevant pollution control equipment. Training be given in emergency response/action plans. The action include the following steps:				✓
	• Only trained personnel who are equipped with protective clothing and equipment shall be allowed to enter the spillage area for clean up.				✓
	• Spills shall be transferred appropriate back into containers using suitable equipment.				✓
	 Absorbent materials shall be used to clean up the spills and shall be disposed of as chemical wastes. 				✓
	 Where appropriate suitable solvents may be used to clean the contaminated area after removal of all contaminated materials. 				✓
	 All necessary protective devices, safety equipment, containers and clean up materials for emergency use shall be maintained to a high standard. 				✓
	3 Spill Clean Up and Disposal				
	Effect the response plan.				✓
	Control the leakage and absorb the spillage using suitably absorbent materials.				
	Provide safety equipment and personal protective equipment for handling of chemical wastes would be similar to that for handling of chemicals.				✓
	Safety equipment includes but is not limited to: • Fire extinguishers.				✓
	• Spades, brushes, dustpan, mop and bucket (or similar readily available on site).				✓
	• Absorbent material such as dry sand, tissues and toweling (all materials readily available on-site).				✓
	Containers including plaster bags, drums, etc.				\checkmark
	Absorbing materials.				✓
	• Pumps.	1			\checkmark
	Personal protective equipment includes as appropriate: • First-aid kits.				\checkmark
	Safety helmet and goggles.				\checkmark
	Gloves which can resist chemical reaction.				\checkmark

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
	Protective boot and clothing.	DSD's	Construction	WQO	✓
5.9.1	Respirators and gas masks.	Contractor	Work Sites		•
	Face visor and masks.				✓
5.9.2	Emergency Responses to Spillages				
	Emergency plans and clean up procedures will need to be provided by the Contractor recognising his specific working methods and construction programme, activities and sequences. Agreement must be sought prior to commencement of the construction work but the following principles should be considered.				
	The emergency plans should include the procedures for:				✓
	spill prevention and precaution;	_			
	response actions; and				✓
	spill clean up and disposal.				✓
	Spill prevention and precaution embraces good site practice and covers:				✓
	good housekeeping practices;				
	chemical storage requirements; and				√
	chemical transfer and transport.				✓
5.9.3	During Operation	DSD's Contractor	Project Area		
	Regular inspection of the tunnels is essential to monitor the structural integrity and proper functioning of the drainage tunnel, which allows repairing of structural deterioration when it begins to develop. It is recommended that routine inspection shall be carried out at least two times per year for the drainage tunnel at the beginning and end of wet season from April to September.				N/A
	Management	_			
6.5.1	During Construction Vegetation Removed from Site Clearance Wastes generated from site clearance shall be sorted and excavated topsoil segregated from roots for re-use in landscaping works, thus eliminating the need for off-site disposal.	DSD's Contractor	Construction Work Sites	Waste Disposal Ordinance (Cap.354); Waste Disposal (Chemical Wastes) (General) Regulation (Cap 354) and ETWBTC No.	✓
	Construction and Demolition Materials The Contractor should reuse any C&D material on-site. C&D waste should be segregated and stored in different containers to other wastes to encourage the re-use or recycling of materials and their proper disposal. The use of wooden hoardings shall not be allowed. An alternative material, which can be reused or recycled, for example, metal (aluminium, alloy, etc) shall be used.			15/2003, Waste anagement on Construction Site	√

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
6.5.1	As referred to the section 6.4.1, the 317,936m ₃ of inert surplus material generated by the project is suitable for public fill. The public fill reception facility at Tuen Mun Area 38 provides a suitable facility for the reuse of surplus inert C&D material generated from the project.	DSD's Contractor	Construction Work Sites	WDO (Cap.354), ETWBTC No. 15/2003, ETWBTC No. 12/2002 and ETWBTC No. 31/2004	
	Under the contract, the contractor will be required to minimise the generation of C&D material and reuse it on site through the following:				
	(a) to plan in the design and construction, methods to minimise the generation of C&D material;				✓
	(b) to submit a Waste Management Plan (WMP) in accordance with Environment Transport and Works Bureau Technical Circular (ETWBTC) No. 15/2003 or any superseding circular(s);	/2003 or any		✓	
	(c) to reuse recycled aggregates in accordance with ETWBTC No. 12/2002 or any superseding circular(s);			✓	
	(d) to observe the requirements of the Trip-Ticket System, stipulated in ETWBTC No. 31/2004 or any superceding circular(s), for disposal of C&D material;				✓
	(e) to incorporate a Waste Management System into the WMP for effective management and control of C&D materials to avoid/reduce/minimise the generation of C&D material during construction.				✓
	The contractor will be required to properly sort into inert C&D materials, metals, timber and other non-inert C&D material in the workplace to prevent cross-contamination.				\checkmark
	In addition, DSD will conduct site inspection to monitor the contractors' performance in the implementation of the WMP and other relevant specified requirements.	DSD	Construction Work Sites	WDO (Cap.354) and ETWBTC No. 15/2003	√
	Excavated Materials Excavated materials should be segregated from other wastes to avoid contamination thereby ensuring acceptability at public filling areas and avoiding the need for disposal at landfill. Municipal Waste	Work Sites ETWBTC No. 15/2003 DSD's Construction WDO (Cap.354) and tion thereby Contractor Work Sites ETWBTC No. 15/2003	√		
	Temporary refuse collection facilities should be set-up by the contractor and wastes should be stored in appropriate containers prior to collection and disposal.				✓
	Domestic effluent generated by the workforce will be directed to foul sewer or chemical toilets if public facilities are not available.				\checkmark
6.5.1	Waste Management Plan A Waste Management Plan (WMP) for the construction of the Project should be prepared as part of the contractors submission. It will provide recommendations for appropriate recycling or disposal route and should include method statement for stockpiling and transportation of the excavated material and other construction wastes should also be included in the WMP and approved before the commencement of construction. All mitigation measures arising from the approved WMP shall be fully implemented.	DSD's Contractor	Construction Work Sites	WDO (Cap.354), ETWBTC No. 15/2003 and ETWBTC No. 33/2002	√

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status
	For the purpose of enhancing the management of C&D material including rock, and to minimize its generation at source, a C&D Material Management Plan (C&DMMP) has been prepared for this project and would be processed in accordance with the Environment, Transport and Works Bureau Technical Circular (Works) No. 33/2002 - Management of Construction and Demolition Material Including Rock.				N/A
Ecology	_			· · · · · · · · · · · · · · · · · · ·	
7.7.1	Avoidance The surface structures are located mainly on existing disturbed areas (ie pollution and urbanisation) and have generally avoided the natural stream sections of higher species diversity and abundance of aquatic organisms.	DSD's Contractor	Construction Work Sites	EIAO	✓
	The major construction activities at streams are scheduled to avoid wet season of high water flow which may adversely affect the downstream natural habitats due to the construction runoff.				✓
7.7.2	Minimisation				
	The previous discussion in Section 7.6.4 has indicated that the impacts on ecological resources due to the construction and operation of the proposed Project are generally expected to be low. The following mitigation measures to minimise impacts and disturbance to the surrounding habitats, are recommended.				✓
	Measures for Construction Runoff Install sheet piles/cofferdam/weir along the boundary of the works area within the stream habitats in particular Sam Dip Tam Stream and Tso Kung Tam Stream before the commencement of works to prevent construction runoff during construction. Provision of adequate designed sand/ silt removal facilities such as sand traps, silt traps and sediment basin in the areas which could potentially be affected may be required.				✓
	Good Construction Practice				✓
	Erect fences along the boundary of the works area before the commencement of works to prevent tipping, vehicle movements, and encroachment of personnel onto adjacent areas, particularly the stream habitats.	DSD's Contractor	Construction Work Sites	EIAO	✓
	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the remaining and surrounding natural stream habitats.				✓
	Regularly check the work site boundaries to ensure that they are not breached and that no damage occurs to surrounding areas.				\checkmark
	Prohibit and prevent open fires within the site boundary during construction and provide temporary fire fighting equipment in the work areas.	_			✓
	Treat any damage that may have occurred to individual major trees in the adjacent area with surgery.				✓

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve?	Status
	Reinstate temporary work sites/disturbed areas, particularly stream of natural bottom and bank, plantation, intertidal habitat, and the areas located within the proposed Ecological Park, immediately after completion of the construction works, ie through on-site tree/shrub planting and reprovision of natural or semi-natural bottom (also refer to Section 7.7.3), in order to facilitate the recolonisation of the wildlife recorded during the baseline surveys. Tree/shrub species used should make reference from those in the surrounding area	DSD's Contractor	Construction Work Sites	EIAO	~
7.7.3	Compensation Provide natural stream bed (approximately 0.03 ha) for the new Dry Weather Flow Channel (created from village-orchard) by laying natural stones at Intake I-2 (Figure 7.7). The reinstated stream bed shall mimic the existing natural conditions with certain portion of big boulders creating the lentic and lotic zones for the aquatic fauna, and while it will be developed during detailed design may draw on concepts shown in Figure 2.18. Provide natural stream bed (approximately 0.5 ha,) for the Approach Channel and Dry				N/A
	Weather Flow Channel by laying natural stones at Intake I-3 (Figure 7.8). The reinstated stream bed shall mimic the existing natural conditions (rocky bottom with very limited aquatic plants) with certain portion of big boulders creating the lentic and lotic zones for the aquatic fauna, and while it will be developed during detailed design may draw on concepts shown in Figure 2.18.				N/A
	Provide natural bottom (ie retain the existing stream bed or reinstate the stream bed by providing boulders/ rocks, riprap or gabion) for the affected stream sections (Figure 7.8) in order to allow natural colonisation of aquatic fauna. Provide at least 2.2 ha of compensatory planting on the permanent and temporary affected				N/A
	plantation areas, particularly the slopes along access road and adjacent to Intake I-3 and cascade at Outfall O-1, after construction to stabilise the slope to present soil erosion and consequent stream sedimentation. Among the 2.2 ha compensatory planting, at least 0.5 ha of compensatory tree planting on the new formed slope along the access road of the Intake I-3 and 0.5 ha of compensatory tree planting over the cascade (by constructing intermediate platform) at Outfall O-1 will be provided (location refer to Figures 7.4 – 7.6). Species used for planting should take reference from the species identified in Appendix F and be native to Hong Kong or South China region.				N/A
	Provide armour rocks for the affected intertidal habitat in order to allow natural colonisation of intertidal organisms.				N/A

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
Cultura	<u>Heritage</u>				
8.6	As no impacts on recorded archaeological sites or area with archaeological potential were identified within the Study Area, no mitigation measure for archaeological resources is considered necessary.				N/A
	The construction methods to be employed should seek to avoid potential vibration impacts to Kuen Yuen Tung Monastery at Lo Wai, the Western Monastery, Yuen Yuen Home for the Aged, Hong Hoi Chee Hong Temple, Chiu Yum Tsing Yuen, Tse's Grave, Wan Lin Bridge and Sam Dip Tam Rock Carving in Sam Dip Tam and the Tin Hau Temple, Yam Kom Tau Village Rural Committee and the Yeung's Ancestral Hall in Yau Kom Tau as these sites fall within 50 m of the Preferred Option of the drainage tunnel alignment or associated Intakes/Outfall construction activities. Construction works that generates excessive vibration in close proximity to these sites should be restricted to protect the building from adverse vibration impacts and to ensure that the building structures will not be damaged as a result of these impacts.	DSD's Contractor	Construction Work Sites	EIAO	N/A
	In order to ensure that no structural or superficial damage will be caused by the construction activities, a precautionary approach involving a pre-construction condition survey and establishment of appropriate vibration limits for the potentially impacted structures should be adopted. Protection measures for the potentially impacted structures, if considered necessary from the pre-construction condition survey, should be implemented prior to the commencement of construction works. Vibration monitoring during the construction phase should be undertaken as part of the EM&A programme.	Qualified archaeologist/ built heritage specialist	Construction Work Sites	EIAO	N/A
<u>Fisherie</u>		•		· · ·	
10.6	In accordance with the guidelines in the <i>EIAO-TM</i> on fisheries impact assessment the general policy for mitigating impacts to fisheries, in order of priority are avoidance, minimization and compensation.	DSD's Contractor	Construction Work Sites	EIAO	N/A
	Impacts to fisheries resources and fishing operations have largely been avoided during the construction and operation of the drainage tunnel through the avoidance of dredging, reclamation and filling activities. Good construction practice and associated measures were recommended in Water Quality Assessment in Section 5 to control water quality impacts to within acceptable levels and are also expected to control impacts to fisheries resources. Hence, no fisheries-species mitigation measures are required during construction and operation of the drainage tunnel.				N/A

Remarks:

√ x Compliance of mitigation measure Non-compliance of mitigation measure Not applicable

N/A

IMPLEMENTATION SCHEDULE August 2008

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status
Air Q	uality				
3.6.1	As mentioned in Section 3.5, exceedances of 1-hour and 24-hour average TSP guideline levels have been predicted at most of the ASRs. Hence, mitigation measures are considered necessary in order to suppress the potential dust impact. The dust suppression measures set out in the <i>Air Pollution Control (Construction Dust)</i>	DSD's Contractor	Construction Work Sites	Air Pollution Control (Construction Dust) Regulation	N/A
	Regulation, in fact, are more extensive. Therefore, it is expected that with watering the construction site every four times daily together with strict implementation of dust suppression measures as stipulated in the Air Pollution Control (Construction Dust) Regulation, the dust level is expected to be reduced by over 75%.				N/A
	General				
	To further ensure compliance with the guideline and AQO limit at the ASRs at all time, it is recommended to implement the <i>Air Pollution Control (Construction Dust) Regulation</i> and include good site practice in the contract clauses to minimize cumulative dust impact. In addition, a comprehensive dust monitoring and audit programme is recommended to ensure proper implementation of the identified mitigation measures. Details of the monitoring and audit requirements are provided in a separate EM&A Manual.				
	• effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building or if a canopy is provided at the first floor level, from the first floor level, up to the highest level of the scaffolding where a scaffolding is erected around the perimeter of a building under construction;				N/A
	• dump truck for material transport should be totally enclosed by impervious sheeting;				✓
	 any excavated dusty materials or stockpile of dusty materials should be covered entirely by impervious sheeting or sprayed with water so as to maintain the entire surface wet, and recovered or backfilled or reinstated within 24 hours of the excavation or unloading; 				✓
	• stockpile of dusty materials should not extend beyond the pedestrian barriers, fencing or traffic cones;				✓
	 dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; 				✓

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
3.6.1	• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;	DSD's Contractor	Construction Work Sites	Air Pollution Control (Construction Dust) Regulation	✓
	 where a site boundary adjoins a road, street or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length except for a site entrance or exit; 				✓
	• every main haul road should be scaled with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet;				✓
	• the portion of road leading only to a construction site that is within 30m of a designated vehicle entrance or exit should be kept clear of dusty materials;				✓
	stockpile of dusty materials should be either covered entirely by impervious sheeting, placed in an area sheltered on the top and the 3 sides; or sprayed with water so as to maintain the entire surface wet;	-			✓
	all dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty material wet;			✓	
	vehicle speed should be limited to 10 kph except on completed access roads;				✓
	• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites;			✓	
	the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle; and				✓
	• the working area of excavation should be sprayed with water immediately before, during and immediately after the operations so as to maintain the entire surface wet.				✓
Noise					
4.6.1	During Construction Appropriate mitigation measures such as the use of quiet equipment and movable barriers will be developed to ensure that noise can be reduced to acceptable levels without causing programme delays	DSD's Contractor	Construction Work Sites	PN 2/93 Noise from Construction Activities & EIAO	N/A
	Good Site Practice Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures should be followed during construction:				
	 only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction works; 				✓
	 machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; 				✓

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve?	Status	
4.6.1	• plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs;	DSD's Contractor	Contractor Work (Construction Dust)		,	✓
	mobile plant should be sited as far away from NSRs as possible; and		Sites	Regulation	\checkmark	
	• material stockpiles and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities.				✓	
	 For Drill and Blast Works Charge mass per delay should be decreased by minimising the number of blastholes firing on each delay. 				N/A	
	Smaller blasthole patterns and longer delays should be used between dependent charges.				N/A	
	Times of blasting should be established to suit the situation and firing blasts when neighbours are busy with their daily tasks (and at a regular time such as lunch time).				N/A	
	 For TBM Tunnelling For the tunnel excavation, it is anticipated that beyond the initial length (say within 30m), excavation will be carried out well within the tunnel and door should be provided to further minimize the noise nuisance to the nearby receivers. 				N/A	
4.6.2	During Operation	DSD's Contractor	Project Area NCO & EIAO	NCO & EIAO		
	Good site practice and noise management can significantly reduce the impact of maintenance activities on nearby NSRs. The following package of measures should be followed during construction					
	only well-maintained plant should be operated on-site;				N/A	
	machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; and					
	• plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs.				N/A	
	Quality					
5.9.1	During Construction	DSD's Contractor	Construction Work Sites	Practice Note for Professional Persons with	✓	
	Mitigation measures and a spill control and response plan have been prepared for works at the intakes and work sites.			regard to site drainage (ProPECC PN 1/94) and		
	Precautions to be taken at any time of year when rainstorms are likely:			WQO	✓	
	 Temporarily exposed surfaces should be covered e.g. by tarpaulin. Temporary access roads should be protected by crushed stone or gravel. 	_			✓	
	Trenches should be dug and backfilled in short sections. Measures should be taken to minimize the ingress of rainwater into trenches.					
	Actions to be taken when a rainstorm is imminent or forecast: • Silt removal facilities, should be checked to ensure that they can function properly.				✓	

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status						
.9.1	 Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric. 	DSD's Contractor		Construction Work Sites	WQO	✓					
	All temporary covers to slopes and stockpiles should be secured.				✓						
	 Actions to be taken during or after rainstorms: Silt removal facilities should be checked and maintained to ensure satisfactory working conditions. 						✓				
	Spill Control and Response Plan										
	1 Prevention and Precaution Measures										
	General PrecautionsNo discharge of silty water into watercourses.				✓						
	 All materials to be used during construction and operation shall be identified and their hazard potential evaluated. 		- - - -					✓			
	 Maintenance of vehicles and equipment involving activities with potential for leakage and spillage shall only be undertaken with the areas appropriately equipped to control these discharges. 					✓					
	 Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials. 								✓		
	 Any construction plant which causes pollution to catchwaters or water gathering ground due to leakage of oil or fuel shall be removed off-site immediately. 										✓
	 Suitable containers shall be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport 								✓		
	 Chemical waste containers shall be suitably labelled to notify and warn the personnel who are handling the wastes to avoid accidents. 							✓			
	• Storage areas shall be selected at safe locations on site and adequate space shall be allocated to the storage area.					✓					
	• Prevent obstructions and tripping hazards.			✓							
	Storage PrecautionsAll chemical storage containers shall be correctly labelled.				✓						
	Solid and impermeable enclosure walls or storage shelves shall be used.]			✓		
	Only compatible chemical wastes shall be stored in the same storage area.						✓				
	• The storage areas shall be inspected to detect any leakages or defective containers on a regular basis.										\checkmark
	• The storage areas shall be inspected to detect any leakages or defective containers on a regular basis.										✓
	• Suitable notices warning of hazards, emergency response plans, telephone numbers etc shall be posted around the site, including storage areas.									✓	
	Large and heavy containers shall be stored at ground level.				✓						

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status
	Chemical waste containers shall be stored below eye level.				✓
5.9.1	Adequate space for handling of the containers shall be provided	DSD's	Construction	WQO	✓
	• Spill response kits shall be located adjacent/near to the storage areas.	Contractor	Work Sites		\checkmark
	A log of chemical wastes shall be maintained.				✓
	Incompatible chemicals shall be stored separately.				✓
	2 Responses/Action Plan				
	All Workers shall be made aware of emergency telephone numbers and the location of all relevant pollution control equipment. Training be given in emergency response/action plans. The action include the following steps:				✓
	• Only trained personnel who are equipped with protective clothing and equipment shall be allowed to enter the spillage area for clean up.				✓
	• Spills shall be transferred appropriate back into containers using suitable equipment.				✓
	 Absorbent materials shall be used to clean up the spills and shall be disposed of as chemical wastes. 				✓
	 Where appropriate suitable solvents may be used to clean the contaminated area after removal of all contaminated materials. 				✓
	 All necessary protective devices, safety equipment, containers and clean up materials for emergency use shall be maintained to a high standard. 				✓
	3 Spill Clean Up and Disposal				
	Effect the response plan.				✓
	Control the leakage and absorb the spillage using suitably absorbent materials.				✓
	Provide safety equipment and personal protective equipment for handling of chemical wastes would be similar to that for handling of chemicals.				✓
	Safety equipment includes but is not limited to: • Fire extinguishers.				✓
	• Spades, brushes, dustpan, mop and bucket (or similar readily available on site).				✓
	• Absorbent material such as dry sand, tissues and toweling (all materials readily available on-site).				✓
	Containers including plaster bags, drums, etc.				\checkmark
	Absorbing materials.				✓
	• Pumps.]			\checkmark
	Personal protective equipment includes as appropriate: • First-aid kits.				\checkmark
	Safety helmet and goggles.				\checkmark
	Gloves which can resist chemical reaction.				\checkmark

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
	Protective boot and clothing.	DSD's	Construction	WQO	✓
5.9.1	Respirators and gas masks.	Contractor	Work Sites		•
	Face visor and masks.				✓
5.9.2	Emergency Responses to Spillages				
	Emergency plans and clean up procedures will need to be provided by the Contractor recognising his specific working methods and construction programme, activities and sequences. Agreement must be sought prior to commencement of the construction work but the following principles should be considered.				
	The emergency plans should include the procedures for:				✓
	spill prevention and precaution;	_			
	response actions; and				✓
	spill clean up and disposal.	_			✓
	Spill prevention and precaution embraces good site practice and covers:				✓
	good housekeeping practices;				
	chemical storage requirements; and				√
	chemical transfer and transport.				✓
5.9.3	During Operation	DSD's Contractor	Project Area		
	Regular inspection of the tunnels is essential to monitor the structural integrity and proper functioning of the drainage tunnel, which allows repairing of structural deterioration when it begins to develop. It is recommended that routine inspection shall be carried out at least two times per year for the drainage tunnel at the beginning and end of wet season from April to September.				N/A
	<u>Management</u>	_			
6.5.1		DSD's Contractor	Construction Work Sites	Waste Disposal Ordinance (Cap.354); Waste Disposal (Chemical Wastes) (General) Regulation (Cap 354) and ETWBTC No.	✓
	Construction and Demolition Materials The Contractor should reuse any C&D material on-site. C&D waste should be segregated and stored in different containers to other wastes to encourage the re-use or recycling of materials and their proper disposal. The use of wooden hoardings shall not be allowed. An alternative material, which can be reused or recycled, for example, metal (aluminium, alloy, etc) shall be used.			15/2003, Waste anagement on Construction Site	√

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status	
6.5.1	As referred to the section 6.4.1, the 317,936m ₃ of inert surplus material generated by the project is suitable for public fill. The public fill reception facility at Tuen Mun Area 38 provides a suitable facility for the reuse of surplus inert C&D material generated from the project.	DSD's Contractor	Construction Work Sites		No. 15/ 2003, ETWBTC No. 12/2002 and ETWBTC No.	
	der the contract, the contractor will be required to minimise the generation of C&D terial and reuse it on site through the following:					
	(a) to plan in the design and construction, methods to minimise the generation of C&D material;				✓	
	(b) to submit a Waste Management Plan (WMP) in accordance with Environment Transport and Works Bureau Technical Circular (ETWBTC) No. 15/2003 or any superseding circular(s);				✓	
	(c) to reuse recycled aggregates in accordance with ETWBTC No. 12/2002 or any superseding circular(s);				✓	
	(d) to observe the requirements of the Trip-Ticket System, stipulated in ETWBTC No. 31/2004 or any superceding circular(s), for disposal of C&D material;	perceding circular(s), for disposal of C&D material; Vaste Management System into the WMP for effective management D materials to avoid/reduce/minimise the generation of C&D onstruction. e required to properly sort into inert C&D materials, metals, timber and			✓	
	(e) to incorporate a Waste Management System into the WMP for effective management and control of C&D materials to avoid/reduce/minimise the generation of C&D material during construction.				✓	
	The contractor will be required to properly sort into inert C&D materials, metals, timber and other non-inert C&D material in the workplace to prevent cross-contamination.				\checkmark	
	In addition, DSD will conduct site inspection to monitor the contractors' performance in the implementation of the WMP and other relevant specified requirements.	DSD	Construction Work Sites	WDO (Cap.354) and ETWBTC No. 15/2003	√	
	Excavated Materials Excavated materials should be segregated from other wastes to avoid contamination thereby ensuring acceptability at public filling areas and avoiding the need for disposal at landfill. Municipal Waste	DSD's Contractor	D's Construction WDO (Cap.354) and	WDO (Cap.354) and	√	
	Temporary refuse collection facilities should be set-up by the contractor and wastes should be stored in appropriate containers prior to collection and disposal.			✓		
	Domestic effluent generated by the workforce will be directed to foul sewer or chemical toilets if public facilities are not available.				\checkmark	
6.5.1	Waste Management Plan A Waste Management Plan (WMP) for the construction of the Project should be prepared as part of the contractors submission. It will provide recommendations for appropriate recycling or disposal route and should include method statement for stockpiling and transportation of the excavated material and other construction wastes should also be included in the WMP and approved before the commencement of construction. All mitigation measures arising from the approved WMP shall be fully implemented.	DSD's Contractor	Construction Work Sites	WDO (Cap.354), ETWBTC No. 15/2003 and ETWBTC No. 33/2002	√	

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status
	For the purpose of enhancing the management of C&D material including rock, and to minimize its generation at source, a C&D Material Management Plan (C&DMMP) has been prepared for this project and would be processed in accordance with the Environment, Transport and Works Bureau Technical Circular (Works) No. 33/2002 - Management of Construction and Demolition Material Including Rock.				N/A
Ecology	_			· · · · · · · · · · · · · · · · · · ·	
7.7.1	Avoidance The surface structures are located mainly on existing disturbed areas (ie pollution and urbanisation) and have generally avoided the natural stream sections of higher species diversity and abundance of aquatic organisms.	DSD's Contractor	Construction Work Sites	EIAO	✓
	The major construction activities at streams are scheduled to avoid wet season of high water flow which may adversely affect the downstream natural habitats due to the construction runoff.				✓
7.7.2	Minimisation				
	The previous discussion in Section 7.6.4 has indicated that the impacts on ecological resources due to the construction and operation of the proposed Project are generally expected to be low. The following mitigation measures to minimise impacts and disturbance to the surrounding habitats, are recommended.				✓
	Measures for Construction Runoff Install sheet piles/cofferdam/weir along the boundary of the works area within the stream habitats in particular Sam Dip Tam Stream and Tso Kung Tam Stream before the commencement of works to prevent construction runoff during construction. Provision of adequate designed sand/ silt removal facilities such as sand traps, silt traps and sediment basin in the areas which could potentially be affected may be required.				✓
	Good Construction Practice				✓
	Erect fences along the boundary of the works area before the commencement of works to prevent tipping, vehicle movements, and encroachment of personnel onto adjacent areas, particularly the stream habitats.	DSD's Contractor	Construction Work Sites	EIAO	✓
	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the remaining and surrounding natural stream habitats.				✓
	Regularly check the work site boundaries to ensure that they are not breached and that no damage occurs to surrounding areas.				\checkmark
	Prohibit and prevent open fires within the site boundary during construction and provide temporary fire fighting equipment in the work areas.	_			✓
	Treat any damage that may have occurred to individual major trees in the adjacent area with surgery.				✓

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve?	Status
	Reinstate temporary work sites/disturbed areas, particularly stream of natural bottom and bank, plantation, intertidal habitat, and the areas located within the proposed Ecological Park, immediately after completion of the construction works, ie through on-site tree/shrub planting and reprovision of natural or semi-natural bottom (also refer to Section 7.7.3), in order to facilitate the recolonisation of the wildlife recorded during the baseline surveys. Tree/shrub species used should make reference from those in the surrounding area	DSD's Contractor	Construction Work Sites	EIAO	~
7.7.3	Compensation Provide natural stream bed (approximately 0.03 ha) for the new Dry Weather Flow Channel (created from village-orchard) by laying natural stones at Intake I-2 (Figure 7.7). The reinstated stream bed shall mimic the existing natural conditions with certain portion of big boulders creating the lentic and lotic zones for the aquatic fauna, and while it will be developed during detailed design may draw on concepts shown in Figure 2.18. Provide natural stream bed (approximately 0.5 ha,) for the Approach Channel and Dry				N/A
	Weather Flow Channel by laying natural stones at Intake I-3 (Figure 7.8). The reinstated stream bed shall mimic the existing natural conditions (rocky bottom with very limited aquatic plants) with certain portion of big boulders creating the lentic and lotic zones for the aquatic fauna, and while it will be developed during detailed design may draw on concepts shown in Figure 2.18.				N/A
	Provide natural bottom (ie retain the existing stream bed or reinstate the stream bed by providing boulders/ rocks, riprap or gabion) for the affected stream sections (Figure 7.8) in order to allow natural colonisation of aquatic fauna. Provide at least 2.2 ha of compensatory planting on the permanent and temporary affected				N/A
	plantation areas, particularly the slopes along access road and adjacent to Intake I-3 and cascade at Outfall O-1, after construction to stabilise the slope to present soil erosion and consequent stream sedimentation. Among the 2.2 ha compensatory planting, at least 0.5 ha of compensatory tree planting on the new formed slope along the access road of the Intake I-3 and 0.5 ha of compensatory tree planting over the cascade (by constructing intermediate platform) at Outfall O-1 will be provided (location refer to Figures 7.4 – 7.6). Species used for planting should take reference from the species identified in Appendix F and be native to Hong Kong or South China region.				N/A
	Provide armour rocks for the affected intertidal habitat in order to allow natural colonisation of intertidal organisms.				N/A

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
Cultural	<u>Heritage</u>				
8.6	As no impacts on recorded archaeological sites or area with archaeological potential were identified within the Study Area, no mitigation measure for archaeological resources is considered necessary.				N/A
	The construction methods to be employed should seek to avoid potential vibration impacts to Kuen Yuen Tung Monastery at Lo Wai, the Western Monastery, Yuen Yuen Home for the Aged, Hong Hoi Chee Hong Temple, Chiu Yum Tsing Yuen, Tse's Grave, Wan Lin Bridge and Sam Dip Tam Rock Carving in Sam Dip Tam and the Tin Hau Temple, Yam Kom Tau Village Rural Committee and the Yeung's Ancestral Hall in Yau Kom Tau as these sites fall within 50 m of the Preferred Option of the drainage tunnel alignment or associated Intakes/Outfall construction activities. Construction works that generates excessive vibration in close proximity to these sites should be restricted to protect the building from adverse vibration impacts and to ensure that the building structures will not be damaged as a result of these impacts.	DSD's Contractor	Construction Work Sites	EIAO	N/A
	In order to ensure that no structural or superficial damage will be caused by the construction activities, a precautionary approach involving a pre-construction condition survey and establishment of appropriate vibration limits for the potentially impacted structures should be adopted. Protection measures for the potentially impacted structures, if considered necessary from the pre-construction condition survey, should be implemented prior to the commencement of construction works. Vibration monitoring during the construction phase should be undertaken as part of the EM&A programme.	Qualified archaeologist/ built heritage specialist	Construction Work Sites	EIAO	N/A
<u>Fisherie</u>					
10.6	In accordance with the guidelines in the <i>EIAO-TM</i> on fisheries impact assessment the general policy for mitigating impacts to fisheries, in order of priority are avoidance, minimization and compensation.	DSD's Contractor	Construction Work Sites	EIAO	N/A
	Impacts to fisheries resources and fishing operations have largely been avoided during the construction and operation of the drainage tunnel through the avoidance of dredging, reclamation and filling activities. Good construction practice and associated measures were recommended in Water Quality Assessment in Section 5 to control water quality impacts to within acceptable levels and are also expected to control impacts to fisheries resources. Hence, no fisheries-species mitigation measures are required during construction and operation of the drainage tunnel.				N/A

Remarks:

√ x Compliance of mitigation measure Non-compliance of mitigation measure Not applicable

N/A

IMPLEMENTATION SCHEDULE September 2008

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
Air Q	uality				
3.6.1	As mentioned in Section 3.5, exceedances of 1-hour and 24-hour average TSP guideline levels have been predicted at most of the ASRs. Hence, mitigation measures are considered necessary in order to suppress the potential dust impact. The dust suppression measures set out in the <i>Air Pollution Control (Construction Dust)</i> Regulation, in fact, are more extensive. Therefore, it is expected that with watering the	DSD's Contractor	Construction Work Sites	Air Pollution Control (Construction Dust) Regulation	N/A
	construction site every four times daily together with strict implementation of dust suppression measures as stipulated in the <i>Air Pollution Control (Construction Dust) Regulation</i> , the dust level is expected to be reduced by over 75%.				N/A
	General				
	To further ensure compliance with the guideline and AQO limit at the ASRs at all time, it is recommended to implement the <i>Air Pollution Control (Construction Dust) Regulation</i> and include good site practice in the contract clauses to minimize cumulative dust impact. In addition, a comprehensive dust monitoring and audit programme is recommended to ensure proper implementation of the identified mitigation measures. Details of the monitoring and audit requirements are provided in a separate EM&A Manual.				
	• effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building or if a canopy is provided at the first floor level, from the first floor level, up to the highest level of the scaffolding where a scaffolding is erected around the perimeter of a building under construction;				N/A
	dump truck for material transport should be totally enclosed by impervious sheeting;				\checkmark
	• any excavated dusty materials or stockpile of dusty materials should be covered entirely by impervious sheeting or sprayed with water so as to maintain the entire surface wet, and recovered or backfilled or reinstated within 24 hours of the excavation or unloading;				✓
	• stockpile of dusty materials should not extend beyond the pedestrian barriers, fencing or traffic cones;				✓
	• dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads;				✓

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status	
3.6.1	• the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;	DSD's Contractor	Construction Work Sites	Air Pollution Control (Construction Dust) Regulation	✓	
	 where a site boundary adjoins a road, street or other area accessible to the public, hoarding of not less than 2.4m high from ground level should be provided along the entire length except for a site entrance or exit; 				✓	
	• every main haul road should be scaled with concrete and kept clear of dusty materials or sprayed with water so as to maintain the entire road surface wet;				✓	
	• the portion of road leading only to a construction site that is within 30m of a designated vehicle entrance or exit should be kept clear of dusty materials;				✓	
	stockpile of dusty materials should be either covered entirely by impervious sheeting, placed in an area sheltered on the top and the 3 sides; or sprayed with water so as to maintain the entire surface wet;				✓	
	all dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty material wet;				✓	
	vehicle speed should be limited to 10 kph except on completed access roads;				✓	
	• every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction sites;				✓	
	the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle; and					✓
	• the working area of excavation should be sprayed with water immediately before, during and immediately after the operations so as to maintain the entire surface wet.				✓	
Noise						
4.6.1	During Construction Appropriate mitigation measures such as the use of quiet equipment and movable barriers will be developed to ensure that noise can be reduced to acceptable levels without causing programme delays	DSD's Contractor	Construction Work Sites	PN 2/93 Noise from Construction Activities & EIAO	N/A	
	Good Site Practice Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures should be followed during construction:					
	 only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction works; 				✓	
	 machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; 				✓	

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve?	Status
4.6.1	• plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs;	DSD's Contractor	Construction Work	Air Pollution Control (Construction Dust)	✓
	mobile plant should be sited as far away from NSRs as possible; and		Sites	Regulation	\checkmark
	• material stockpiles and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities.				✓
	 For Drill and Blast Works Charge mass per delay should be decreased by minimising the number of blastholes firing on each delay. 				N/A
	Smaller blasthole patterns and longer delays should be used between dependent charges.				N/A
	Times of blasting should be established to suit the situation and firing blasts when neighbours are busy with their daily tasks (and at a regular time such as lunch time).				N/A
	 For TBM Tunnelling For the tunnel excavation, it is anticipated that beyond the initial length (say within 30m), excavation will be carried out well within the tunnel and door should be provided to further minimize the noise nuisance to the nearby receivers. 				N/A
4.6.2	During Operation	DSD's Contractor	Project Area	NCO & EIAO	
	Good site practice and noise management can significantly reduce the impact of maintenance activities on nearby NSRs. The following package of measures should be followed during construction	-			
	only well-maintained plant should be operated on-site;				N/A
	machines and plant that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; and				N/A
	• plant known to emit noise strongly in one direction should, where possible, be orientated to direct noise away from the NSRs.				N/A
	Quality				
5.9.1	During Construction	DSD's Contractor	Construction Work Sites	Practice Note for Professional Persons with	✓
	Mitigation measures and a spill control and response plan have been prepared for works at the intakes and work sites.			regard to site drainage (ProPECC PN 1/94) and	
	Precautions to be taken at any time of year when rainstorms are likely:			WQO	✓
	 Temporarily exposed surfaces should be covered e.g. by tarpaulin. Temporary access roads should be protected by crushed stone or gravel. 				✓
	Trenches should be dug and backfilled in short sections. Measures should be taken to minimize the ingress of rainwater into trenches.				✓
	Actions to be taken when a rainstorm is imminent or forecast: • Silt removal facilities, should be checked to ensure that they can function properly.				✓

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status											
.9.1	• Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric.	DSD's Contractor	Construction Work Sites	WQO	✓											
	All temporary covers to slopes and stockpiles should be secured.				✓											
	Actions to be taken during or after rainstorms: Silt removal facilities should be checked and maintained to ensure satisfactory working conditions.				✓											
	Spill Control and Response Plan															
	1 Prevention and Precaution Measures															
	General PrecautionsNo discharge of silty water into watercourses.				✓											
	 All materials to be used during construction and operation shall be identified and their hazard potential evaluated. 				✓											
	 Maintenance of vehicles and equipment involving activities with potential for leakage and spillage shall only be undertaken with the areas appropriately equipped to control these discharges. 	-														✓
	 Any soil contaminated with chemicals/oils shall be removed from site and the void created shall be filled with suitable materials. 					✓										
	 Any construction plant which causes pollution to catchwaters or water gathering ground due to leakage of oil or fuel shall be removed off-site immediately. 							✓								
	 Suitable containers shall be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport 						✓									
	 Chemical waste containers shall be suitably labelled to notify and warn the personnel who are handling the wastes to avoid accidents. 				✓											
	• Storage areas shall be selected at safe locations on site and adequate space shall be allocated to the storage area.				✓											
	• Prevent obstructions and tripping hazards.				✓											
	Storage PrecautionsAll chemical storage containers shall be correctly labelled.				\checkmark											
	• Solid and impermeable enclosure walls or storage shelves shall be used.				✓											
	• Only compatible chemical wastes shall be stored in the same storage area.			✓												
	• The storage areas shall be inspected to detect any leakages or defective containers on a regular basis.						✓									
	 The storage areas shall be inspected to detect any leakages or defective containers on a regular basis. 			✓												
	• Suitable notices warning of hazards, emergency response plans, telephone numbers etc shall be posted around the site, including storage areas.					✓										
	Large and heavy containers shall be stored at ground level.				✓											

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status	
	Chemical waste containers shall be stored below eye level.				✓	
5.9.1	Adequate space for handling of the containers shall be provided	DSD's	Construction	WQO	√	
	• Spill response kits shall be located adjacent/near to the storage areas.	Contractor	Work Sites		\checkmark	
	A log of chemical wastes shall be maintained.				✓	
	Incompatible chemicals shall be stored separately.				✓	
	2 Responses/Action Plan					
	All Workers shall be made aware of emergency telephone numbers and the location of all relevant pollution control equipment. Training be given in emergency response/action plans. The action include the following steps:				✓	
	• Only trained personnel who are equipped with protective clothing and equipment shall be allowed to enter the spillage area for clean up.				✓	
	• Spills shall be transferred appropriate back into containers using suitable equipment.				✓	
	 Absorbent materials shall be used to clean up the spills and shall be disposed of as chemical wastes. 				✓	
	 Where appropriate suitable solvents may be used to clean the contaminated area after removal of all contaminated materials. 				✓	
	 All necessary protective devices, safety equipment, containers and clean up materials for emergency use shall be maintained to a high standard. 				✓	
	3 Spill Clean Up and Disposal					
	Effect the response plan.				✓	
	Control the leakage and absorb the spillage using suitably absorbent materials.				\checkmark	
	Provide safety equipment and personal protective equipment for handling of chemical wastes would be similar to that for handling of chemicals.				✓	
	Safety equipment includes but is not limited to: • Fire extinguishers.				✓	
	• Spades, brushes, dustpan, mop and bucket (or similar readily available on site).				✓	
	• Absorbent material such as dry sand, tissues and toweling (all materials readily available on-site).				✓	
	Containers including plaster bags, drums, etc.				\checkmark	
	Absorbing materials.	_			\checkmark	
	• Pumps.				\checkmark	
	Personal protective equipment includes as appropriate: • First-aid kits.					✓
	Safety helmet and goggles.				\checkmark	
	Gloves which can resist chemical reaction.				\checkmark	

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
	Protective boot and clothing.	DSD's	Construction	WQO	✓
5.9.1	Respirators and gas masks.	Contractor	Work Sites		•
	Face visor and masks.				✓
5.9.2	Emergency Responses to Spillages				
	Emergency plans and clean up procedures will need to be provided by the Contractor recognising his specific working methods and construction programme, activities and sequences. Agreement must be sought prior to commencement of the construction work but the following principles should be considered.				
	The emergency plans should include the procedures for:				✓
	spill prevention and precaution;	_			
	response actions; and				✓
	spill clean up and disposal.				✓
	Spill prevention and precaution embraces good site practice and covers:				✓
	good housekeeping practices;	_			
	chemical storage requirements; and				√
	chemical transfer and transport.				✓
5.9.3	During Operation	DSD's Contractor	Project Area		
	Regular inspection of the tunnels is essential to monitor the structural integrity and proper functioning of the drainage tunnel, which allows repairing of structural deterioration when it begins to develop. It is recommended that routine inspection shall be carried out at least two times per year for the drainage tunnel at the beginning and end of wet season from April to September.				N/A
	<u>Management</u>	_			
6.5.1	During Construction Vegetation Removed from Site Clearance Wastes generated from site clearance shall be sorted and excavated topsoil segregated from roots for re-use in landscaping works, thus eliminating the need for off-site disposal.	DSD's Contractor	Construction Work Sites	Waste Disposal Ordinance (Cap.354); Waste Disposal (Chemical Wastes) (General) Regulation (Cap 354) and ETWBTC No.	✓
	Construction and Demolition Materials The Contractor should reuse any C&D material on-site. C&D waste should be segregated and stored in different containers to other wastes to encourage the re-use or recycling of materials and their proper disposal. The use of wooden hoardings shall not be allowed. An alternative material, which can be reused or recycled, for example, metal (aluminium, alloy, etc) shall be used.			15/2003, Waste anagement on Construction Site	√

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve ?	Status	
6.5.1	As referred to the section 6.4.1, the 317,936m3 of inert surplus material generated by the project is suitable for public fill. The public fill reception facility at Tuen Mun Area 38 provides a suitable facility for the reuse of surplus inert C&D material generated from the project.	DSD's Contractor	Construction Work Sites	WDO (Cap.354), ETWBTC No. 15/ 2003, ETWBTC No. 12/2002 and ETWBTC No. 31/2004		
	Under the contract, the contractor will be required to minimise the generation of C&D material and reuse it on site through the following:					
	(a) to plan in the design and construction, methods to minimise the generation of C&D material;				✓	
	(b) to submit a Waste Management Plan (WMP) in accordance with Environment Transport and Works Bureau Technical Circular (ETWBTC) No. 15/2003 or any superseding circular(s);				✓	
	(c) to reuse recycled aggregates in accordance with ETWBTC No. 12/2002 or any superseding circular(s);				✓	
	(d) to observe the requirements of the Trip-Ticket System, stipulated in ETWBTC No. 31/2004 or any superceding circular(s), for disposal of C&D material;	uirements of the Trip-Ticket System, stipulated in ETWBTC No.			✓	
	(e) to incorporate a Waste Management System into the WMP for effective management and control of C&D materials to avoid/reduce/minimise the generation of C&D material during construction.				✓	
	The contractor will be required to properly sort into inert C&D materials, metals, timber and other non-inert C&D material in the workplace to prevent cross-contamination.				\checkmark	
	In addition, DSD will conduct site inspection to monitor the contractors' performance in the implementation of the WMP and other relevant specified requirements.	DSD	Construction Work Sites	WDO (Cap.354) and ETWBTC No. 15/2003	√	
	Excavated Materials Excavated materials should be segregated from other wastes to avoid contamination thereby ensuring acceptability at public filling areas and avoiding the need for disposal at landfill. Municipal Waste	DSD's Contractor	Construction Work Sites	Construction WDO (Cap.354) and	WDO (Cap.354) and	√
	Temporary refuse collection facilities should be set-up by the contractor and wastes should be stored in appropriate containers prior to collection and disposal.				✓	
	Domestic effluent generated by the workforce will be directed to foul sewer or chemical toilets if public facilities are not available.				✓	
6.5.1	Waste Management Plan A Waste Management Plan (WMP) for the construction of the Project should be prepared as part of the contractors submission. It will provide recommendations for appropriate recycling or disposal route and should include method statement for stockpiling and transportation of the excavated material and other construction wastes should also be included in the WMP and approved before the commencement of construction. All mitigation measures arising from the approved WMP shall be fully implemented.	DSD's Contractor	Construction Work Sites	WDO (Cap.354), ETWBTC No. 15/2003 and ETWBTC No. 33/2002	√	

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure?	Location of the measure	What requirements or standards for the measure to achieve?	Status
	For the purpose of enhancing the management of C&D material including rock, and to minimize its generation at source, a C&D Material Management Plan (C&DMMP) has been prepared for this project and would be processed in accordance with the Environment, Transport and Works Bureau Technical Circular (Works) No. 33/2002 - Management of Construction and Demolition Material Including Rock.				N/A
Ecology	_			· · · · · · · · · · · · · · · · · · ·	
7.7.1	Avoidance The surface structures are located mainly on existing disturbed areas (ie pollution and urbanisation) and have generally avoided the natural stream sections of higher species diversity and abundance of aquatic organisms.	DSD's Contractor	Construction Work Sites	EIAO	✓
	The major construction activities at streams are scheduled to avoid wet season of high water flow which may adversely affect the downstream natural habitats due to the construction runoff.				✓
7.7.2	Minimisation				
	The previous discussion in Section 7.6.4 has indicated that the impacts on ecological resources due to the construction and operation of the proposed Project are generally expected to be low. The following mitigation measures to minimise impacts and disturbance to the surrounding habitats, are recommended.				✓
	Measures for Construction Runoff Install sheet piles/cofferdam/weir along the boundary of the works area within the stream habitats in particular Sam Dip Tam Stream and Tso Kung Tam Stream before the commencement of works to prevent construction runoff during construction. Provision of adequate designed sand/ silt removal facilities such as sand traps, silt traps and sediment basin in the areas which could potentially be affected may be required.				✓
	Good Construction Practice				✓
	Erect fences along the boundary of the works area before the commencement of works to prevent tipping, vehicle movements, and encroachment of personnel onto adjacent areas, particularly the stream habitats.	DSD's Contractor	Construction Work Sites	EIAO	✓
	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the remaining and surrounding natural stream habitats.				✓
	Regularly check the work site boundaries to ensure that they are not breached and that no damage occurs to surrounding areas.				\checkmark
	Prohibit and prevent open fires within the site boundary during construction and provide temporary fire fighting equipment in the work areas.	_			✓
	Treat any damage that may have occurred to individual major trees in the adjacent area with surgery.				✓

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve?	Status
	Reinstate temporary work sites/disturbed areas, particularly stream of natural bottom and bank, plantation, intertidal habitat, and the areas located within the proposed Ecological Park, immediately after completion of the construction works, ie through on-site tree/shrub planting and reprovision of natural or semi-natural bottom (also refer to Section 7.7.3), in order to facilitate the recolonisation of the wildlife recorded during the baseline surveys. Tree/shrub species used should make reference from those in the surrounding area	DSD's Contractor	Construction Work Sites	EIAO	√
7.7.3	Compensation Provide natural stream bed (approximately 0.03 ha) for the new Dry Weather Flow Channel (created from village-orchard) by laying natural stones at Intake I-2 (Figure 7.7). The reinstated stream bed shall mimic the existing natural conditions with certain portion of big boulders creating the lentic and lotic zones for the aquatic fauna, and while it will be developed during detailed design may draw on concepts shown in Figure 2.18. Provide natural stream bed (approximately 0.5 ha,) for the Approach Channel and Dry				N/A
	Weather Flow Channel by laying natural stones at Intake I-3 (Figure 7.8). The reinstated stream bed shall mimic the existing natural conditions (rocky bottom with very limited aquatic plants) with certain portion of big boulders creating the lentic and lotic zones for the aquatic fauna, and while it will be developed during detailed design may draw on concepts shown in Figure 2.18.				N/A
	Provide natural bottom (ie retain the existing stream bed or reinstate the stream bed by providing boulders/ rocks, riprap or gabion) for the affected stream sections (Figure 7.8) in order to allow natural colonisation of aquatic fauna. Provide at least 2.2 ha of compensatory planting on the permanent and temporary affected				N/A
	plantation areas, particularly the slopes along access road and adjacent to Intake I-3 and cascade at Outfall O-1, after construction to stabilise the slope to present soil erosion and consequent stream sedimentation. Among the 2.2 ha compensatory planting, at least 0.5 ha of compensatory tree planting on the new formed slope along the access road of the Intake I-3 and 0.5 ha of compensatory tree planting over the cascade (by constructing intermediate platform) at Outfall O-1 will be provided (location refer to Figures 7.4 – 7.6). Species used for planting should take reference from the species identified in Appendix F and be native to Hong Kong or South China region.				N/A
	Provide armour rocks for the affected intertidal habitat in order to allow natural colonisation of intertidal organisms.				N/A

EIA Ref.	Recommended Mitigation Measures	Who to implement the measure ?	Location of the measure	What requirements or standards for the measure to achieve ?	Status
Cultural	<u>Heritage</u>				
8.6	As no impacts on recorded archaeological sites or area with archaeological potential were identified within the Study Area, no mitigation measure for archaeological resources is considered necessary.				N/A
	The construction methods to be employed should seek to avoid potential vibration impacts to Kuen Yuen Tung Monastery at Lo Wai, the Western Monastery, Yuen Yuen Home for the Aged, Hong Hoi Chee Hong Temple, Chiu Yum Tsing Yuen, Tse's Grave, Wan Lin Bridge and Sam Dip Tam Rock Carving in Sam Dip Tam and the Tin Hau Temple, Yam Kom Tau Village Rural Committee and the Yeung's Ancestral Hall in Yau Kom Tau as these sites fall within 50 m of the Preferred Option of the drainage tunnel alignment or associated Intakes/Outfall construction activities. Construction works that generates excessive vibration in close proximity to these sites should be restricted to protect the building from adverse vibration impacts and to ensure that the building structures will not be damaged as a result of these impacts.	DSD's Contractor	Construction Work Sites	EIAO	N/A
	In order to ensure that no structural or superficial damage will be caused by the construction activities, a precautionary approach involving a pre-construction condition survey and establishment of appropriate vibration limits for the potentially impacted structures should be adopted. Protection measures for the potentially impacted structures, if considered necessary from the pre-construction condition survey, should be implemented prior to the commencement of construction works. Vibration monitoring during the construction phase should be undertaken as part of the EM&A programme.	Qualified archaeologist/ built heritage specialist	Construction Work Sites	EIAO	N/A
<u>Fisherie</u>					
10.6	In accordance with the guidelines in the <i>EIAO-TM</i> on fisheries impact assessment the general policy for mitigating impacts to fisheries, in order of priority are avoidance, minimization and compensation.	DSD's Contractor	Construction Work Sites	EIAO	N/A
	Impacts to fisheries resources and fishing operations have largely been avoided during the construction and operation of the drainage tunnel through the avoidance of dredging, reclamation and filling activities. Good construction practice and associated measures were recommended in Water Quality Assessment in Section 5 to control water quality impacts to within acceptable levels and are also expected to control impacts to fisheries resources. Hence, no fisheries-species mitigation measures are required during construction and operation of the drainage tunnel.				N/A

Remarks:

√ x Compliance of mitigation measure Non-compliance of mitigation measure Not applicable

N/A



Appendix E

Monitoring Locations

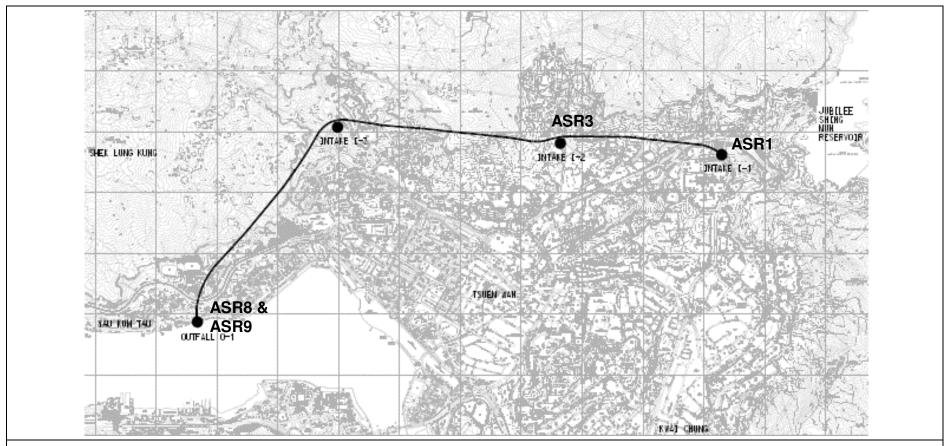


Figure 1 Air Quality Monitoring Stations

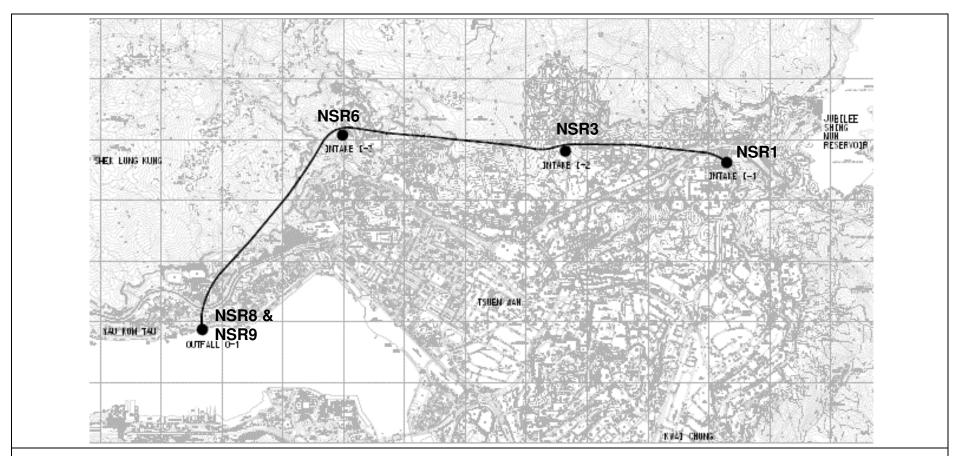


Figure 2 Noise Monitoring Stations



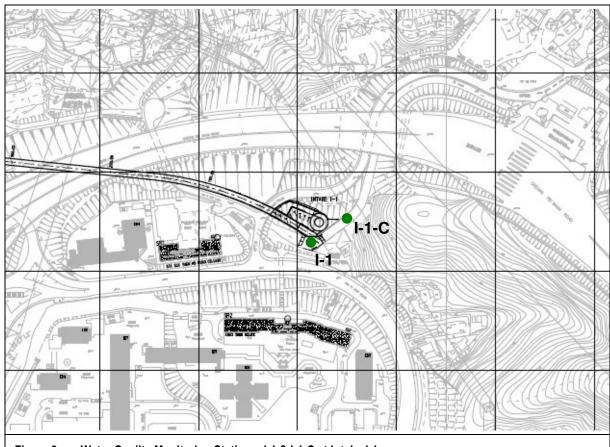


Figure 3 Water Quality Monitoring Stations: I-1 & I-1-C at Intake I-1

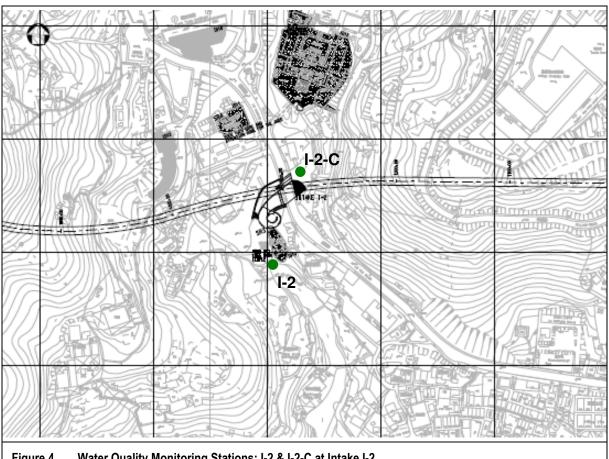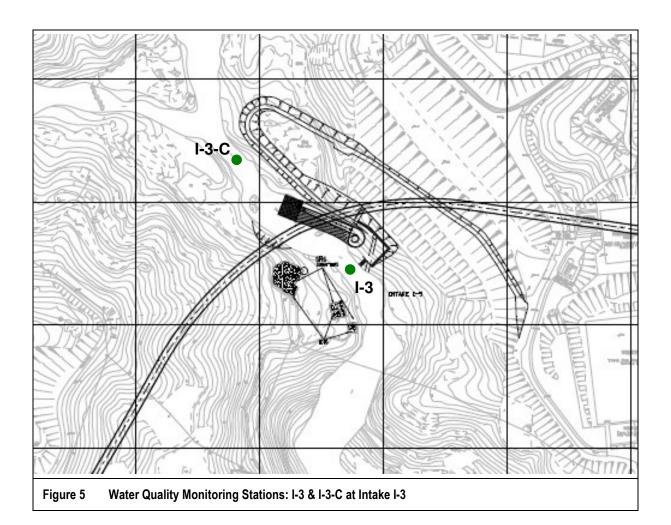

Water Quality Monitoring Stations: I-2 & I-2-C at Intake I-2 Figure 4



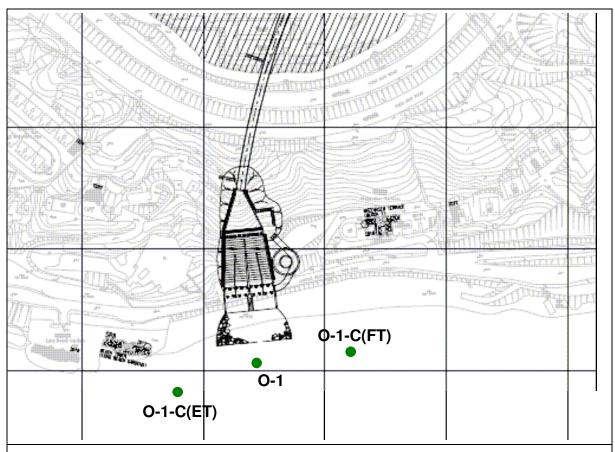



Figure 6 Water Quality Monitoring Stations: O-1, O-1-C(ET) & O-1-C(FT) at Outfall O-1




Appendix F

Monitoring Results

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Air Quality Monitoring (1-hr TSP) Results at Sik Sik Yuen Ho Fung College - Intake (ASR1) Jul-08 to Sep-08

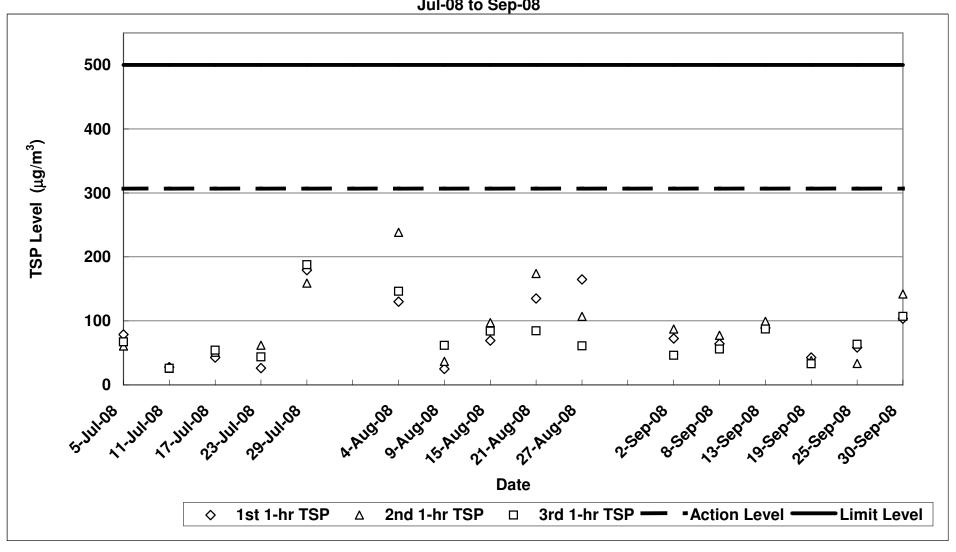


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Air Quality Monitoring (1-hr TSP) Results at Hong Hoi Chee Hong Temple - Intake (ASR3) Jul-08 to Sep-08

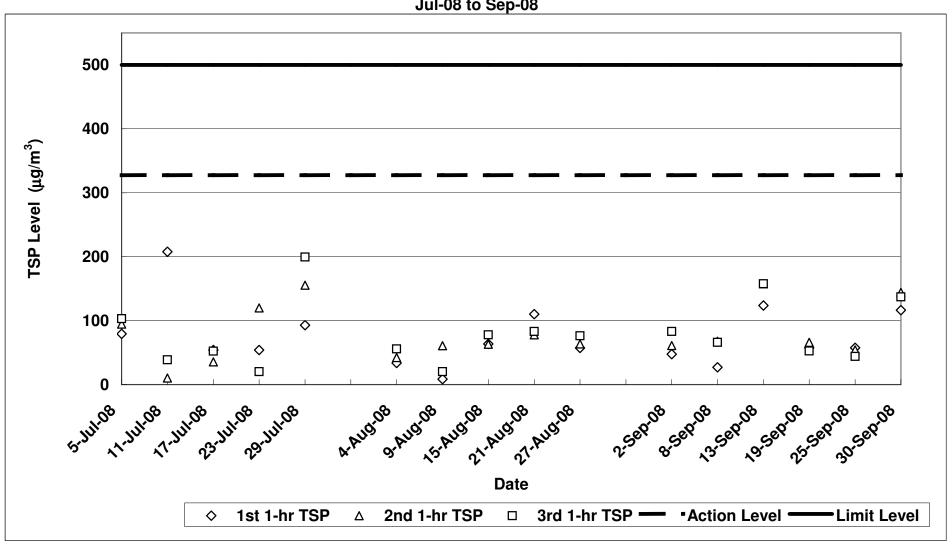


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Air Quality Monitoring (1-hr TSP) Results at Long Beach Gardens - Outfall (ASR8)

Jul-08 to Sep-08

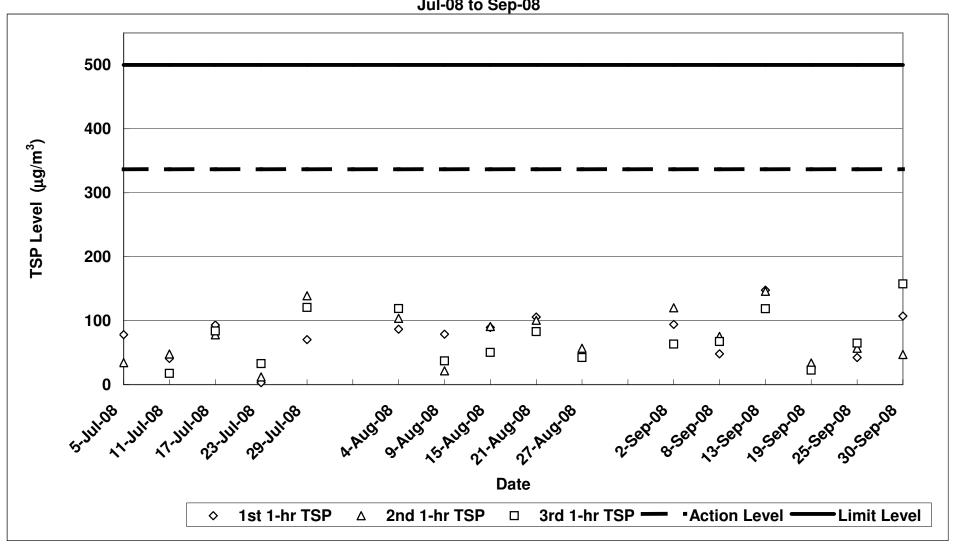


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Air Quality Monitoring (1-hr TSP) Results at Greenview Terrance - Outfall (ASR9)


Jul-08 to Sep-08

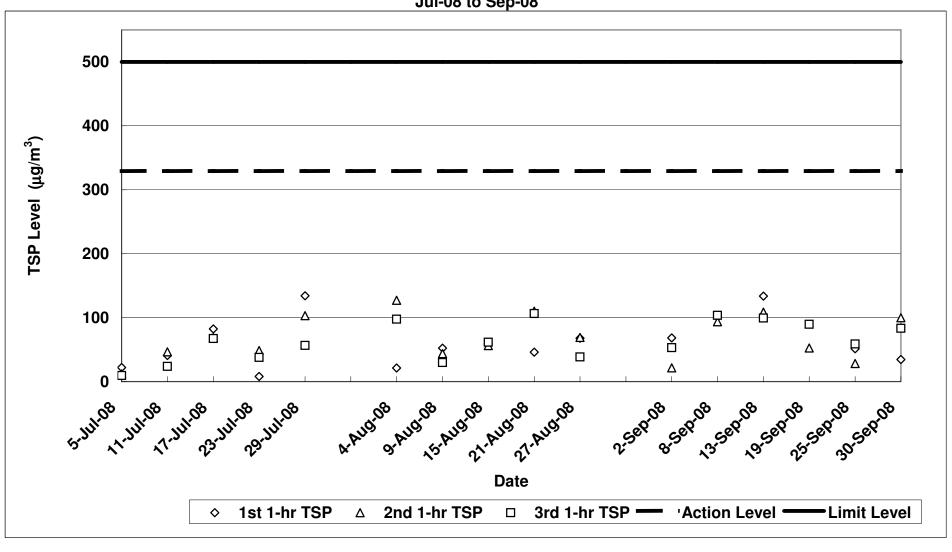


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Noise Monitoring Results at Sik Sik Yuen Ho Fung College (NSR 1)

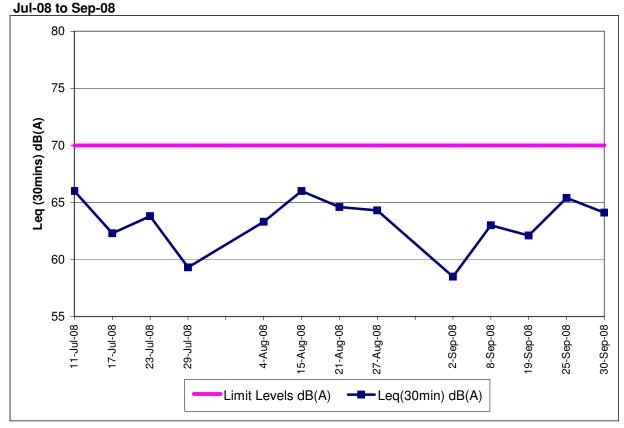


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Noise Monitoring Results at Hong Hoi Chee Hong Temple (NSR 3) Jul-08 to Sep-08

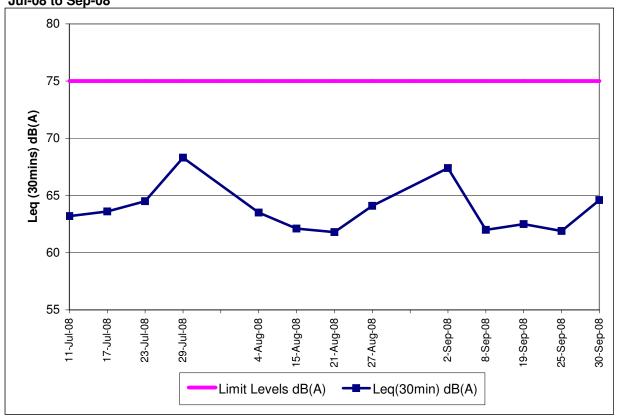


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Noise Monitoring Results at Squatters (NSR 6)

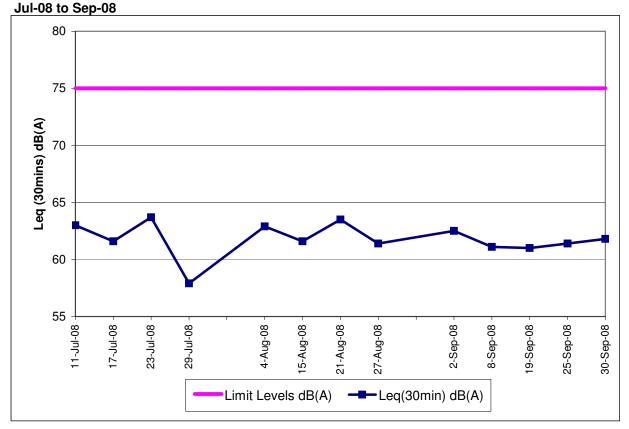


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Noise Monitoring Results at Long Beach Gardens (NSR 8)

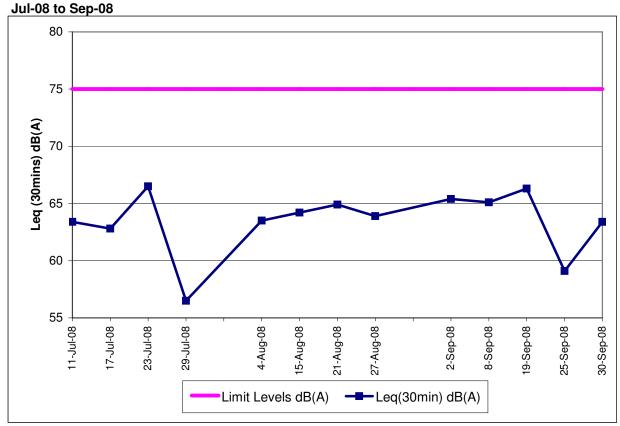


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Noise Monitoring Results at Greenview Terrace (NSR 9) $\,$

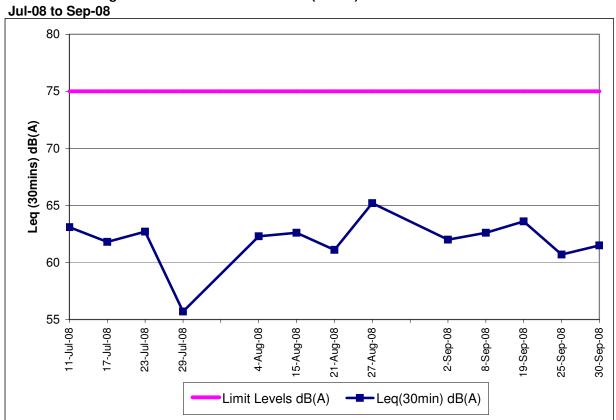


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1)

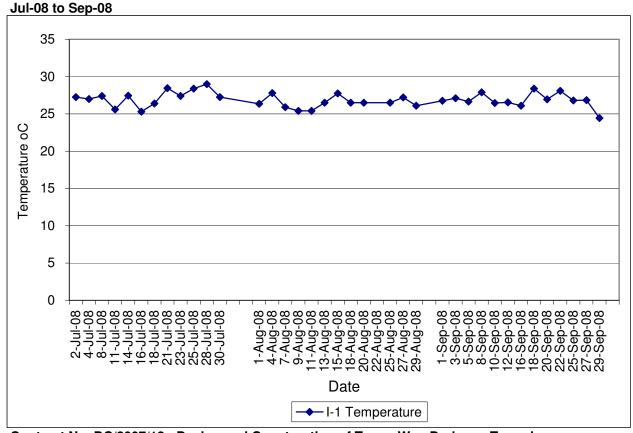


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C) Jul-08 to Sep-08

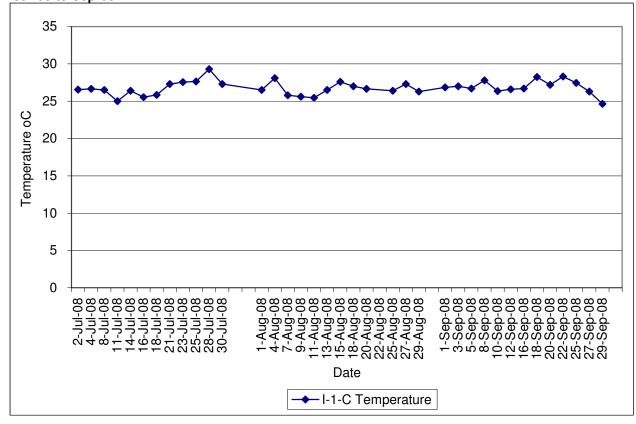


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2) Jul-08 to Sep-08

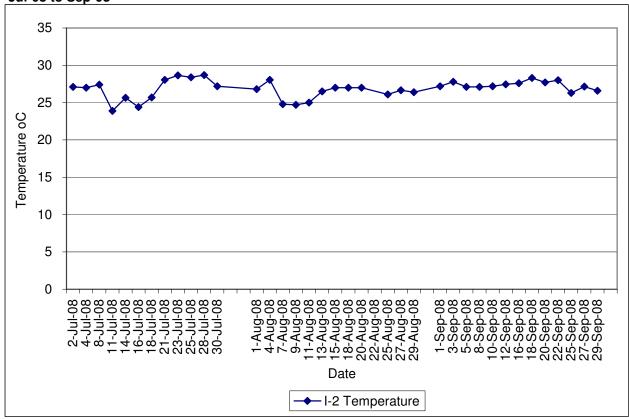


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C) Jul-08 to Sep-08

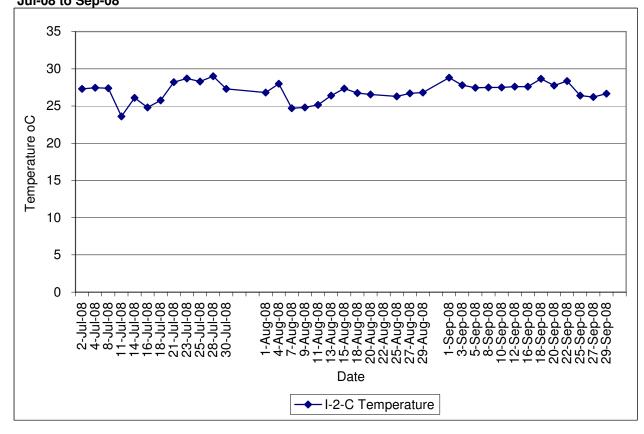


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3)

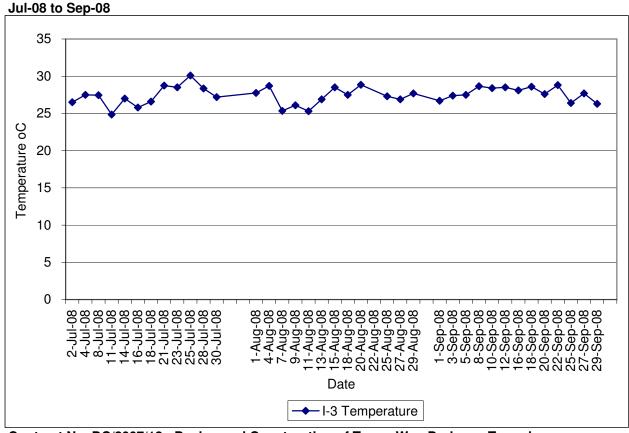


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3-C) Jul-08 to Sep-08

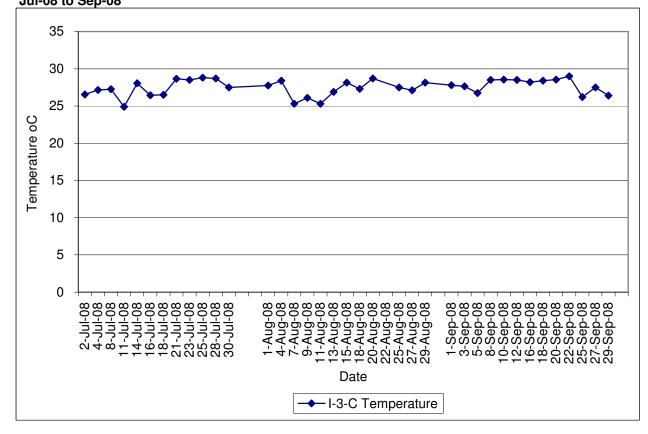


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1)

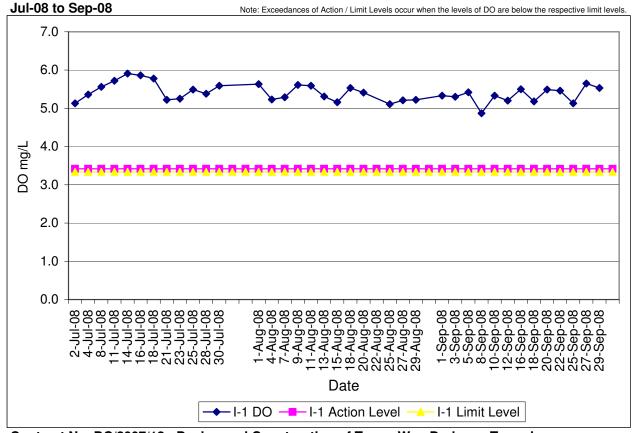


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C) Jul-08 to Sep-08

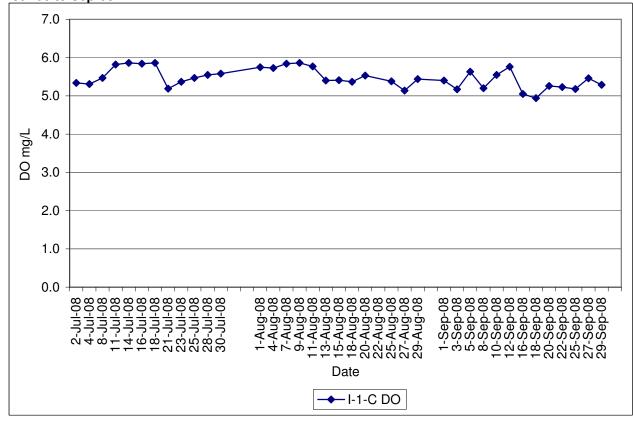


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2)

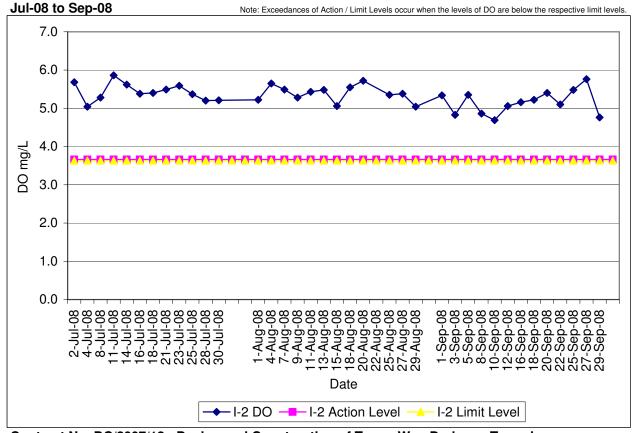


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C) Jul-08 to Sep-08

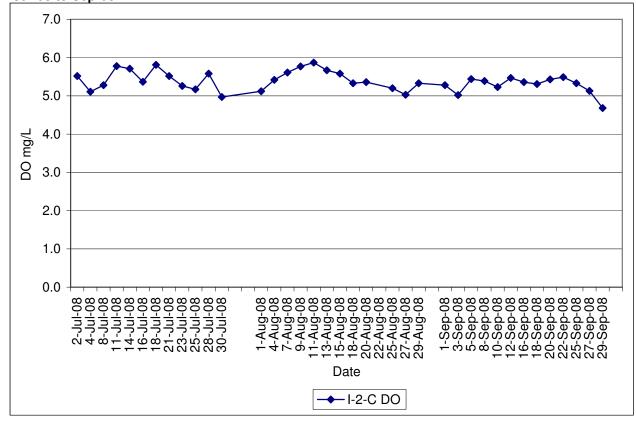


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3)

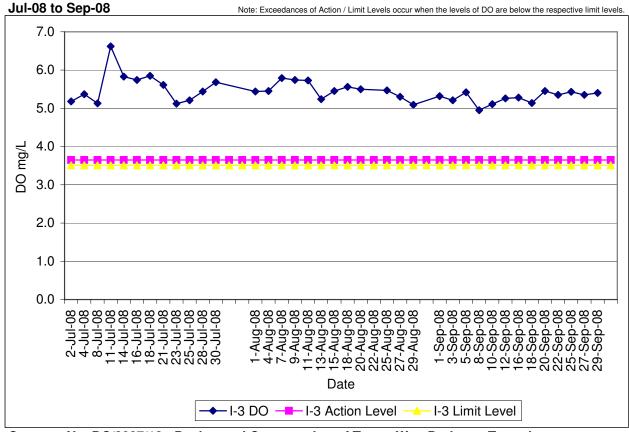


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3-C)

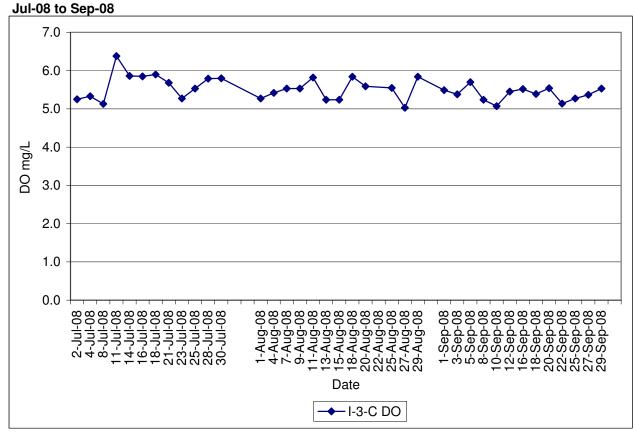


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1) Jul-08 to Sep-08

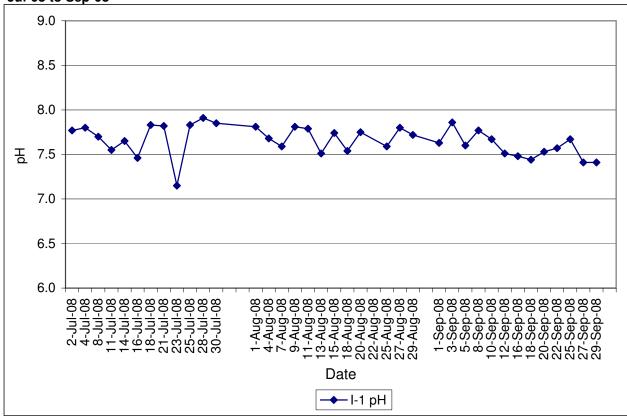


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C) Jul-08 to Sep-08

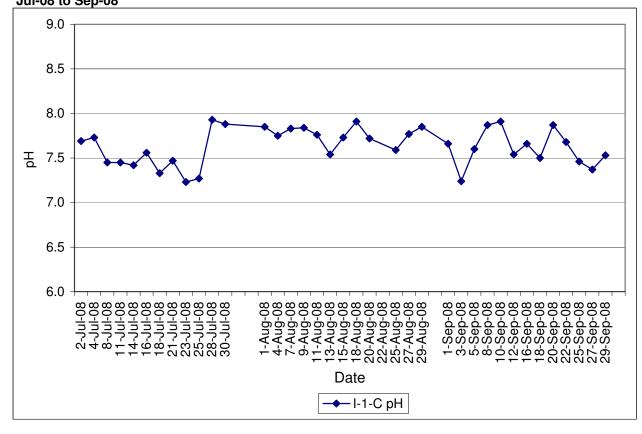


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2) Jul-08 to Sep-08

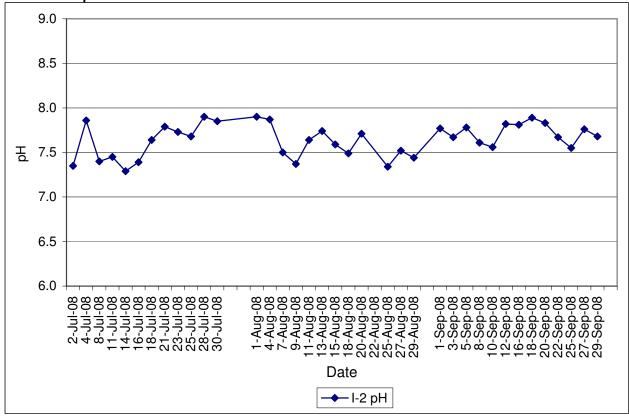


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C) Jul-08 to Sep-08

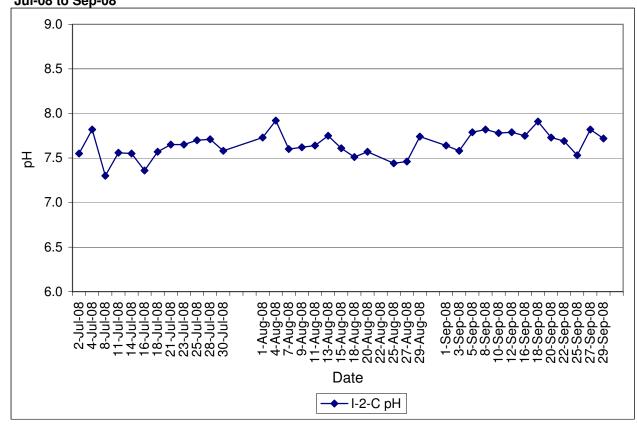


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3)

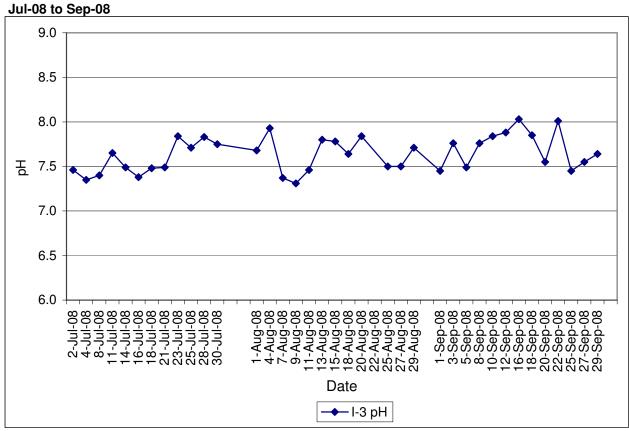


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3-C) Jul-08 to Sep-08

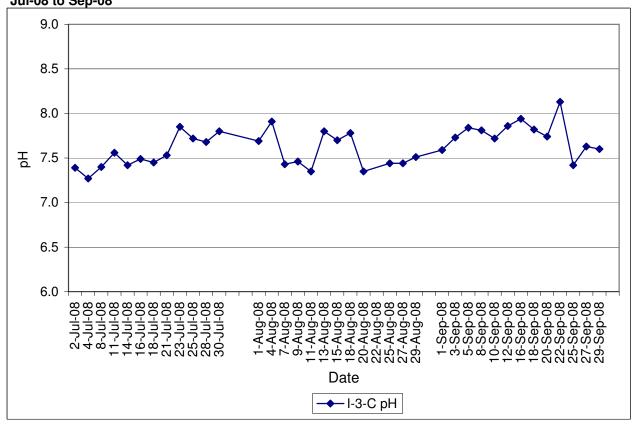


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1) Jul-08 to Sep-08

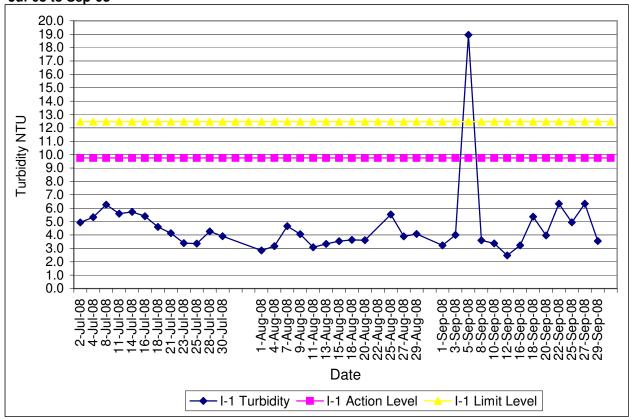


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C) Jul-08 to Sep-08

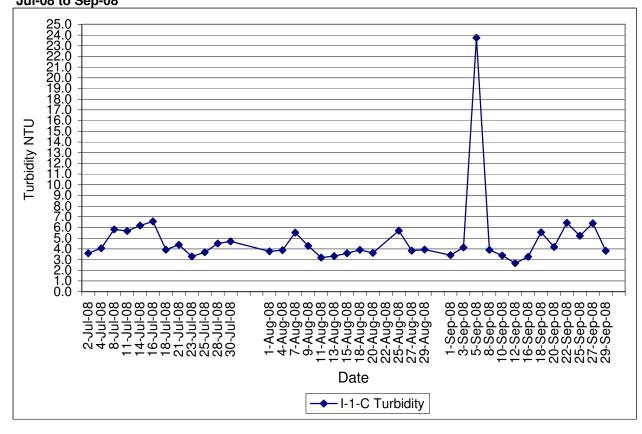


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2)

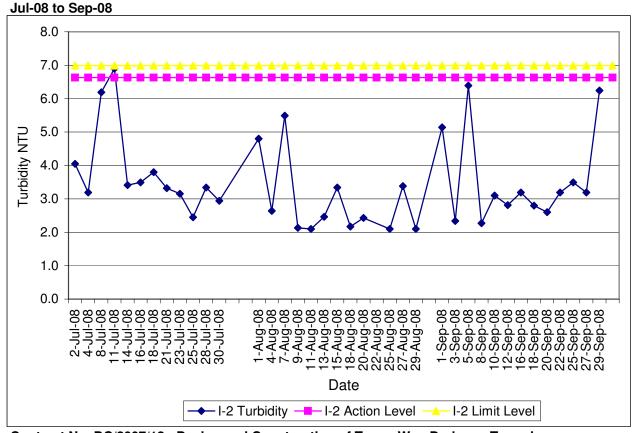


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C) Jul-08 to Sep-08

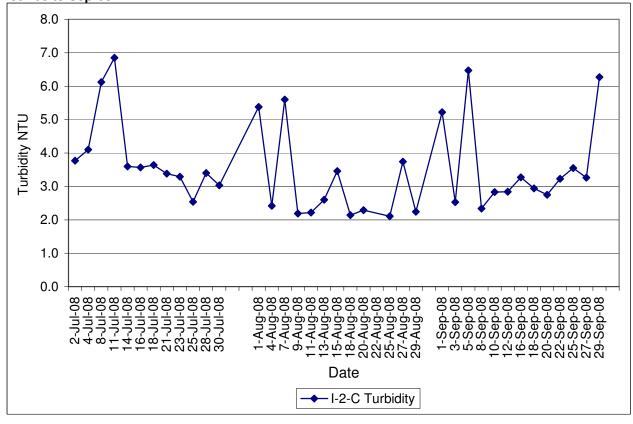


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3)

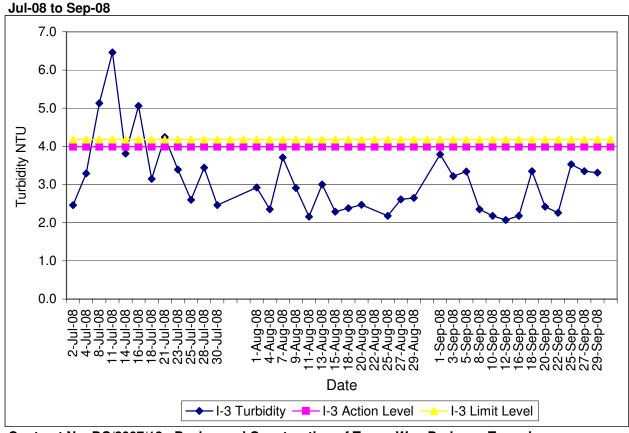


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3-C)

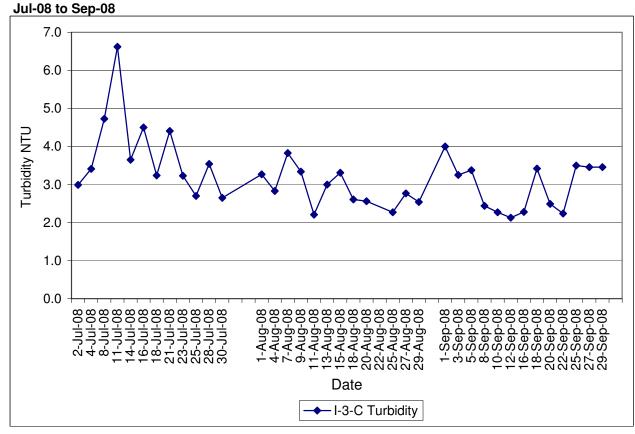


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1) Jul-08 to Sep-08

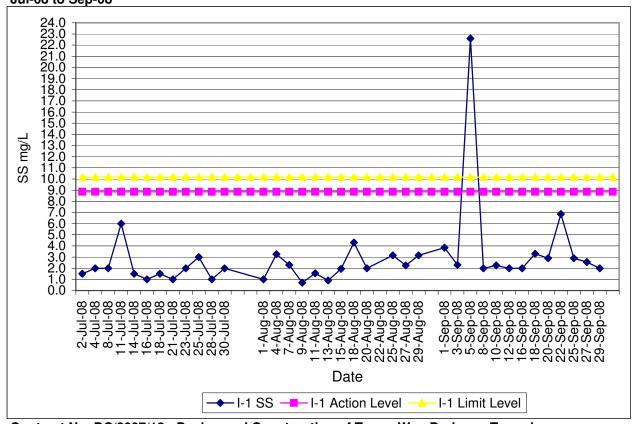


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Sik Sik Yuen Ho Fung College (I-1-C) Jul-08 to Sep-08

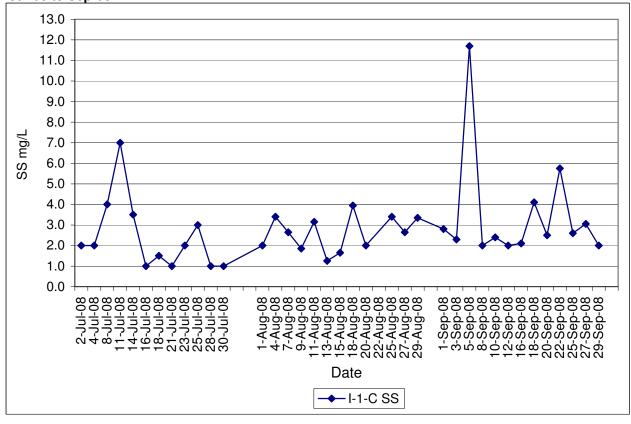


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2)

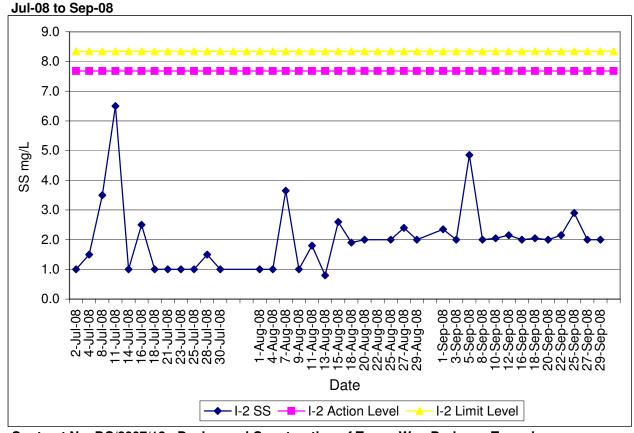


Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Hong Hoi Chee Hong Temple (I-2-C) Jul-08 to Sep-08

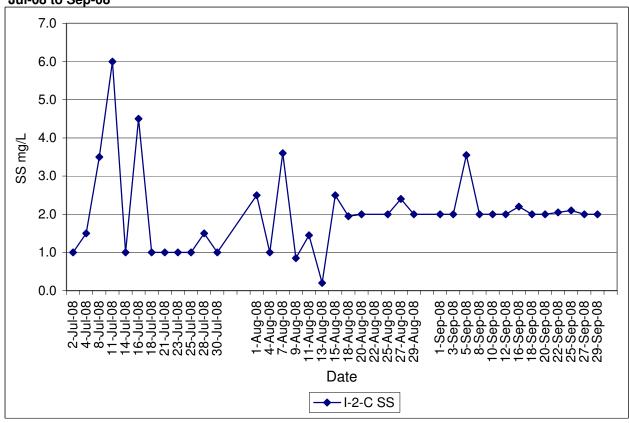

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3)

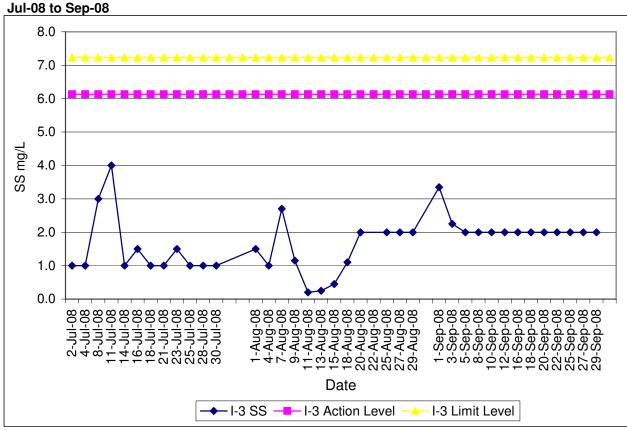

Contract No. DC/2007/12 - Design and Construction of Tsuen Wan Drainage Tunnel Water Quality Results at Squatters (I-3-C)

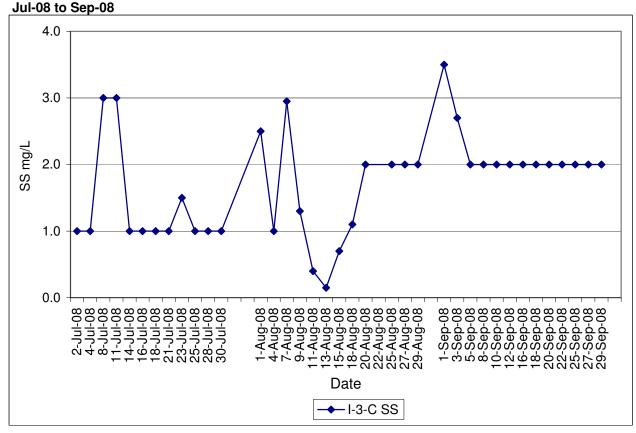



Appendix G

Interim Notifications of Environmental Quality Limits

Exceedances

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	2-Jul-08
Time	12:18 PM
Monitoring Location	Sik Sik Yuen Ho Fung College (I-1)
Parameter	Turbidity
Action & Limit Levels	9.75 / 12.47
Measured Level	4.94 (higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low Turbidity level of 3.60 is recorded at Control Station (I-1-C)
Actions taken / to be taken	No construction activitiy is recorded. Exceedances is not project related. No follow up action.
Remarks	The action level exceedance is considered not project-related.

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Downd Chan

25-Jul-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	4-Jul-08
Time	12:16 PM
Monitoring Location	Sik Sik Yuen Ho Fung College (I-1)
Parameter	Turbidity
Action & Limit Levels	9.75 / 12.47
Measured Level	5.33 (higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low Turbidity level of 4.06 is recorded at Control Station (I-1-C)
Actions taken / to be taken	No construction activitiy is recorded. Exceedances is not project related. No follow up action.
Remarks	The action level exceedance is considered not project-related.

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Down of Chan

25-Jul-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	8-Jul-08
Time	12:16 PM
Monitoring Location	Squatters (I-3)
Parameter	Turbidity
Action & Limit Levels	3.99 / 4.18
Measured Level	5.13
Possible reason for Action or Limit Level Non-compliance	Natural variation
Actions taken / to be taken	Similar level is recorded at Control Station, this exceedance is not project related. No follow up action.
Remarks	Only minor construction activitiy (U-channel preparation at the entrance) is recorded.

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Dogwood Chan

25-Jul-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	11-Jul-08
Time	12:13 PM
Monitoring Location	Hong Hoi Chee Hong Temple (I-2)
Parameter	Turbidity
Action & Limit Levels	6.63 / 6.99
Measured Level	6.90
Possible reason for Action or Limit Level Non-compliance	Natural variation
Actions taken / to be taken	Similar level is recorded at Control Station, this exceedance is not project related. No follow up action.
Remarks	Only minor construction activitiy (leveling of working platform) is recorded.

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Commod Chan

25-Jul-08

Date:

Desmond Chan

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	11-Jul-08
Time	2:50 PM
Monitoring Location	Squatters (I-3)
Parameter	Turbidity
Action & Limit Levels	3.99 / 4.18
Measured Level	6.46
Possible reason for Action or Limit Level Non-compliance	Natural variation
Actions taken / to be taken	Similar level is recorded at Control Station, this exceedance is not project related. No follow up action.
Remarks	Only minor construction activitiy(Hoarding erection)

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Dosmond Chan
Date:	25-Jul-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	16-Jul-08
Time	4:12 PM
Monitoring Location	Squatters (I-3)
Parameter	Turbidity
Action & Limit Levels	3.99 / 4.18
Measured Level	5.06
Possible reason for Action or Limit Level Non-compliance	Natural variation
Actions taken / to be taken	Similar level is recorded at Control Station, this exceedance is not project related. No follow up action.
Remarks	Only minor construction activitiy(Hoarding erection)

Prepared by:

Desmond Chan

Designation:

Environmental Consultant

Deemod Chan

Signature:

25-Jul-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	21-Jul-08
Time	4:12 PM
Monitoring Location	Squatters (I-3)
Parameter	Turbidity
Action & Limit Levels	3.99 / 4.18
Measured Level	4.24
Possible reason for Action or Limit Level Non-compliance	Natural variation
Actions taken / to be taken	Similar level is recorded at Control Station, this exceedance is not project related. No follow up action.
Remarks	Only minor construction activitiy(Hoarding erection & Transplantation)

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Town of Chan

25-Jul-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	11-Jul-08
Time	2:50 PM
Monitoring Location	Squatters (I-3)
Parameter	Suspended Solid
Action & Limit Levels	6.13 / 7.23
Measured Level	4.00 (higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low Turbidity level of 3.00 is recorded at Control Station (I-3-C)
Actions taken / to be taken	Only minor construction activity (hoarding erection). Exceedances is not project related. No follow up action.
Remarks	The action level exceedance is considered not project-related.

Designation:	Environmental Consultant
Signature:	Domond Chan

25-Jul-08

Desmond Chan

Prepared by:

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	16-Jul-08
Time	4:12 PM
Monitoring Location	Squatters (I-3)
Parameter	Suspended Solid
Action & Limit Levels	6.13 <i>/</i> 7.23
Measured Level	1.50 (higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low Turbidity level of 1.00 is recorded at Control Station (I-3-C)
Actions taken / to be taken	Only minor construction activity (hoarding erection). Exceedances is not project related. No follow up action.
Remarks	The action level exceedance is considered not project-related.

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Lasmond Cham,
Date:	25-Jul-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	30-Jul-08
Time	1:26 PM
Monitoring Location	Sik Sik Yuen Ho Fung College (I-1)
Parameter	Suspended Solid
Action & Limit Levels	8.85 / 10.17
Measured Level	2.00 (higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low SS level of 1.00 is recorded at Control Station (I-1-C)
Actions taken / to be taken	Construction activities include hoarding erection, soil nailing and steel bridge formation). Exceedances is not project related. No follow up action.
Remarks	The action level exceedance is considered not project-related.

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Leamond Chan

6-Aug-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	11-Aug-08
Time	10:59 AM
Monitoring Location	Hong Hoi Chee Hong Temple (I-2)
Parameter	Suspended Solid
Action & Limit Levels	7.68 / 8.34
Measured Level	1.8 (higher than 120% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low SS level of 1.45 is recorded at Control Station (I-2-C)
Actions taken / to be taken	The measured SS levels at both impact & control stations were well below the Action Level of baseline measurement and no direct disturbance was observed contributed by project construction activities (levelling of piling platform). There is no evidence to show the exceedance is project-related and no action is considered necessary.
Remarks	The action level exceedance is considered not to be project-related.

Prepared by:

Antony Wong

Designation:

Environmental Team Leader

Signature:

Date:

20-Aug-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	13-Aug-08
Time	10:50 AM
Monitoring Location	Hong Hoi Chee Hong Temple (I-2)
Parameter	Suspended Solid
Action & Limit Levels	7.68 / 8.34
Measured Level	0.8(higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low SS level of 0.2 is recorded at Control Station (I-2-C)
Actions taken / to be taken	No action is required as the monitoring result was well below both Action & Limit Levels and no direct disturbance was observed contributed by project construction activities (levelling of piling platform). There is no evidence to show the exceedance is project-related
Remarks	The limit level exceedance is considered not project-related.

Prepared by:

Antony Wong

Designation:

Environmental Team Leader

Signature:

Date:

25-Aug-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	13-Aug-08
Time	11:58 AM
Monitoring Location	Squatters (I-3)
Parameter	Suspended Solid
Action & Limit Levels	6.13 / 7.23
Measured Level	0.25(higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low SS level of 0.15 is recorded at Control Station (I-3-C)
Actions taken / to be taken	No action is required as the monitoring result was well below both Action & Limit Levels and no direct disturbance was observed contributed by project construction activities (site tidying & cleaning and removal of dead trees). There is no evidence to show the exceedance is project-related
Remarks	The limit level exceedance is considered not project-related.

Prepared by:

Antony Wong

Designation:

Environmental Team Leader

Signature:

Date:

25-Aug-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	01-Sep-08
Time	9:02am
Monitoring Location	Sik Sik Yuen Ho Fung College (I-1)
Parameter	Suspended Solid
Action & Limit Levels	8.85 / 10.17
Measured Level	3.9 (higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	A low SS level of 2.8 is recorded at Control Station (I-1-C)
Actions taken / to be taken	No action is required as the monitoring result was well below both Action & Limit Levels and no direct disturbance was observed contributed by project construction activities (tree transplant, soil nail & mobilization of constructional plants). There is no evidence to show the exceedance is project-related. No exceedance was recorded for measurement performed on 3/9/2008.
Remarks	The limit level exceedance is considered not project-related.

Designation:	Senior Environmental Consultant
Signature:	e can not their

Desmond Chan

Date: 11-Sep-08

Prepared by:

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	05-Sep-08
Time	9:07am
Monitoring Location	Sik Sik Yuen Ho Fung College (I-1)
Parameter	Turbidity
Action & Limit Levels	9.75 / 12.47
Measured Level	18.95
Possible reason for Action or Limit Level Non-compliance	Muddy water was observed generated from other CEDD's project (Yick Hing) at upper steam regarding to site investigation. Refer to attached photos for details
Actions taken / to be taken	No action is required as the result of monitoring station was below the control station and no direct disturbance was observed contributed by the project construction activities.
Remarks	The limit level exceedance is considered not to be project-related.

Prepared by:	Desmond Chan
Designation:	Environmental Consultant
Signature:	Daniond Chan
Date:	08-Sep-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	05-Sep-08
Time	10:55am
Monitoring Location	Hong Hoi Chee Hong Temple (I-2)
Parameter	Suspended Solid
Action & Limit Levels	7.68 / 8.34
Measured Level	4.9 (higher than 130% of control control station's SS)
Possible reason for Action or Limit Level Non-compliance	No construction work except mobilization of geological investigation plant was observed on site during measurement. Exceedance may be possibly caused by air pipe leakage of air compressor from other project (GE/2006/17) regarding site inspection on 5 September 2008. (see attached photo)
Actions taken / to be taken	The Contractor is requested to contact the Contractor of Project GE/2006/17 to fix the air pipe as soon as possible. No exceedance was recorded for measurement performed on 8/9/2008.
Remarks	The limit level exceedance is considered not project-related.

Prepared b	γy.	
------------	-----	--

Desmond Chan

Designation:

Senior Environmental Consultant

Desent Chan

Signature:

Date: 16-Sep-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	05-Sep-08
Time	10:55am
Monitoring Location	Sik Sik Yuen Ho Fung College (I-1)
Parameter	Suspended Solid
Action & Limit Levels	8.85 / 10.17
Measured Level	22.6
Possible reason for Action or Limit Level Non-compliance	Muddy water was observed generated from CEDD's project (Yick Hing) at upper steam regarding to site investigation. Refer to attached photos for details
Actions taken / to be taken	No action is taken as the result of monitoring station was below the control station and no direct disturbance was observed contributed by the project construction activities.
Remarks	The limit level exceedance is considered not to be project-related.

Prepared by:	Desmond Chan
Designation:	Senior Environmental Consultant
Signature:	Chan Chan

16-Sep-08

Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel
Date	5-Sep-08
Time	10:55am
Monitoring Location	Sik Sik Yuen Ho Fung College (I-1)
Parameter	Suspended Solid
Action & Limit Levels	8.85 / 10.17
Measured Level	22.6
Possible reason for Action or Limit Level Non-compliance	No construction work of this project was undertaken during measurement. Muddy runoff was observed from another CEDD's construction site and the runoff discharged to the upstream of the impact monitoring station I-1.
Actions taken / to be taken	No action was considered to be necessary as exceedance was likely to be caused by the mentioned runoff, the SS exceedance is unlikely to be project-related.
Remarks	The limit level exceedance is considered not to be project-related.

Hemarks	The limit level exceedance is considered not to be projective
Prepared by:	Desmond Chan
Designation:	Senior Environmental Consultant
Signature:	Dogwood Chan

9/16/2008 (revised on 15 October)

Photographic record for exceedance of Suspended Solid recorded at Sik Sik Yuen Ho Fung College (I-1) on 05-Sep-08





Incident Report on Action Level or Limit Level Non-compliance

Project	Tsuen Wan Drainage Tunnel	
Date	25-Sep-08	
Time	10:35 AM	
Monitoring Location	Hong Hoi Chee Hong Temple (I-2)	
Parameter	Suspended Solid	
Action & Limit Levels	7.68 / 8.34	
Measured Level	2.9 (higher than 130% of control control station's SS)	
Possible reason for Action or Limit Level Non-compliance	A low SS level of 2.1 is recorded at Control Station (I-2-C)	
Actions taken / to be taken	No action is taken as the monitoring result was well below both Action & Limit Levels and no direct disturbance was observed contributed by project construction activities (ground investigation). There is no evidence to show the exceedance is project-related. No exceedance was recorded for measurement performed on 27/9/2008.	
Remarks	The control limit level exceedance is considered not project-related.	

Prepared by:	Desmond Chan
Designation:	Senior Environmental Consultant
Signature:	Comond Chan

08-Oct-08

Photographic record for exceedance of Suspended Solid recorded at Hong Hoi Chee Hong Temple (I-2) on 25-Sep-08



