

AUES JOB NO.: TCS00715/14

TUEN MUN - CHEK LAP KOK LINK Contract No. HY/2013/12 – Northern Connection Toll Plaza and Associated Works

## 28<sup>th</sup> Monthly Environmental Monitoring and Audit (EM&A) Report – February 2017

PREPARED FOR CRBC and Kaden Joint Venture

Date	<b>Reference No.</b>	<b>Prepared By</b>	Certified By
8 March 2017	TCS00715/14/600/R0278v2	Ben Tam	T.W. Tam (Environmental Team Leader)



Ref.: HYDHZMBEEM00\_0\_5144L.17

10 March 2017

By Fax (2293 6300) and By Post

AECOM Supervising Officer Representative's Office No. 8 Mong Fat Street, Tuen Mun, New Territories, Hong Kong

Attention: Mr. Albert Yu

Dear Mr. Yu,

## Re: Agreement No. CE 48/2011 (EP) Environmental Project Office for the HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing Facilities, and Tuen Mun-Chek Lap Kok Link – Investigation

Contract No. HY/2013/12 TM-CLKL Northern Connection Toll Plaza and Associated Works 28<sup>th</sup> Monthly EM&A Report for February 2017 (EP-354/2009/D)

Reference is made to the Monthly Environmental Monitoring and Audit (EM&A) Report (Feb. 2017) (AUES reference: TCS00715/14/600/R0278v2 dated 8 March 2017) certified by the ET Leader and provided to us via e-mail on 10 March 2017.

Please be informed that we have no adverse comments on the captioned monthly EM&A report. We write to verify the captioned submission in accordance with Condition 4.4 of EP-354/2009/D.

Thank you for your attention. Please do not hesitate to contact the undersigned or the ENPO Leader Mr. Y. H. Hui should you have any queries.

Yours sincerely,

Hanf Fanlblong

F. C. Tsang Independent Environmental Checker Tuen Mun – Chek Lap Kok Link

c.c.

HyD – Mr. Stephen Chan (By Fax: 3188 6614) HyD – Mr. Vico Cheung (By Fax: 3188 6614) AECOM – Mr. Conrad Ng (By Fax: 3922 9797) AUES – Mr. T. W. Tam (By Fax: 2959 6079) CRBC – Kaden JV – Mr. John Wong (By Fax: 2253 8399)

Internal: DY, YH, ENPO Site

Q:\Projects\HYDHZMBEEM00\02\_Proj\_Mgt\02\_Corr\HYDHZMBEEM00\_0\_5144L.17.docx

Ramboll Environ Hong Kong Limited 英環香港有限公司 21/F, BEA Harbour View Centre, 56 Gloucester Road, Wan Chai, Hong Kong Tel: 852.3465 2888 Fax: 852.3465 2899 www.Ramboll-Environ.com



## EXECUTIVE SUMMARY

ES01 This is the 28<sup>th</sup> Monthly EM&A Report presenting the monitoring results and inspection findings for the period from 1 to 28 February 2017 (hereinafter 'the Reporting Period').

## SUMMARY OF EM&A ACTIVITIES FOR THE REPORTING PERIOD

- ES02 The EM&A activities conducted in the Reporting Period are summary in below:-
  - 24-hours TSP of Air Quality Monitoring –45 events
  - 1-hour TSP of Air Quality Monitoring **135 events**
  - Cultural Heritage Inspection **5 events**
  - Landfill Gas Monitoring 24 days
  - Landscape & Visual Monitoring 4 events
  - Environmental Site Inspection 5 events

### **BREACH OF ACTION AND LIMIT (A/L) LEVELS**

ES03 In the Reporting Period, no exceedances of 1-hour and 24-hour TSP were recorded according to the measurement results by the ET of Contract HY/2012/08. The summary of breach of air quality performance is shown below.

Environmentel	Monitoring	Action	I imit	Event & Action		n
Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	NOE Issued	Investigation	Corrective Actions
A in Onality	1-hour TSP	0	0	0	0	0
Air Quality	24-hour TSP	0	0	0	0	0

- ES04 No noise complaints were received in the Reporting Period.
- ES05 Landfill gas monitoring was conducted at the TD1 and Lung Mun Road works area in this reporting month by the Safety Officer. The monitoring results shown no exceedances were triggered.
- ES06 Site inspection for landscape and visual was conducted on weekly basis by the Landscape Architect to ensure the compliance with the intended aims of the mitigation measures. Most of the landscape works such as planting was not yet commenced.

## SITE INSPECTION

- ES07 In the Reporting Period, joint site inspection by the RE, ET and the Contractor was carried out on 2<sup>nd</sup>, 7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> February 2017 and the IEC has attended the joint site inspection on 28<sup>th</sup> February 2017. No non-compliance was recorded during the site inspection but 1 observation and 4 reminders were recorded.
- ES08 Inspection for Pitcher Plants of ecology and grave of culture heritage were also carried out during the weekly site inspection. It was observed that the transplanted pitcher plants were properly protected. Establishment period for the pitcher plants was completed at the end of September 2016 and the final pitcher plants report was submitted to AFCD on early December 2016. Since then only the integrity of the protection fence was checked to fulfil the EIA requirement.

## **ENVIRONMENTAL COMPLAINT**

ES09 In the Reporting Period, no environmental complaint was received.



ES10 The statistical summary of environmental complaints is summarized in the following table.

Departing Deviad	<b>Environmental Complaint Statistics</b>		
Reporting Period	Frequency	Cumulative	
Since the Contract commencement	7	7	
February 2017	0	7	

### NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES11 No environmental summons or successful prosecutions were recorded in the Reporting Period.

### **REPORTING CHANGE**

ES12 No reporting changes were made in the Reporting Period.

### **FUTURE KEY ISSUES**

- ES13 During dry season, air quality mitigation measures such as watering of site area for 12 times per day and covering of exposed slopes should be fully implemented to reduce construction dust impact as recommended in the EMIS.
- ES14 Moreover, muddy water or other water pollutants from site surface runoff into the public areas will be key environment issue. Special attention should be paid on the water quality mitigation measures to prevent surface runoff flow to public area.
- ES15 It was reminded that good housekeeping practice should be maintained. Mosquito control measures should be properly implemented to prevent mosquito breeding on site especially after rain.



## TABLE OF CONTENTS

1	INTRODU	CTION				1
		CONTRACT BACKGROUND				1
	1.2 F	REPORT STRUCTURE				1
2	CONTRAC	T ORGANIZATION	AND	CONSTRUCTION	PROGRESS	AND
		MENTAL SUBMISSIONS				2
		CONTRACT ORGANIZATION				2
		CONSTRUCTION PROGRESS				2
		UMMARY OF ENVIRONMENTA				2
3		OF IMPACT MONITORI	NG REQ	UIREMENTS UNDER	THE CONTRA	
		GENERAL				3
		AIR QUALITY MONITORING				3 3 3
		IONITORING EDUCATION				3
		IONITORING EQUIPMENT				4
		DERIVATION OF ACTION/LIMIT	(A/L)L	EVELS		5
		OTHER ENVIRONMENTAL ASPI				5
	3.8 N	IONITORING SCHEDULE				6
4	AIR OUAL	ITY MONITORING				7
-		GENERAL				7
	4.2 A	AIR QUALITY MONITORING RE	ESULTS IN	NREPORTING PERIOD		7
		ACTION AND LIMIT (A/L) LEV				7
	4.4 A	AIR QUALITY EXCEEDANCE IN	IVESTIGA	TION		7
5	ECOLOGY	MONITORING				8
	5.1 C	JENERAL				8
	5.2 F	TITCHER PLANTS INSPECTION				8
6	CULTURA	L HERITAGE				9
		JENERAL				9
	6.2 C	<b>GRAVE INSPECTION</b>				9
7	LANDSCAL	PE AND VISUAL				10
	7.1 C	General				10
	7.2 L	ANDSCAPE AND VISUAL INSP	ECTION			10
8	LANDFILL	GAS HAZARD MONITOI	RING			11
	8.1 C	GENERAL				11
	8.2 L	ANDFILL GAS MONITORING F	RESULT			11
9	WASTE MA	ANAGEMENT				13
-		GENERAL WASTE MANAGEME	NT			13
	9.2 F	RECORDS OF WASTE QUANTIT	IES			13
10	INSPECTIO	ON AND AUDIT				14
10		ITE INSPECTION				14
11	ENVIRON	MENTAL COMPLAINT AN	JD NON	-COMPLIANCE		16
11		ENVIRONMENTAL COMPLAINT				16
10						
12		NTATION STATUS OF MI	IIGATI	UN MEASURES		17
		GENERAL REQUIREMENTS		ς ινίτμε ζομίνο Μοντμ		17 17
		ENTATIVE CONSTRUCTION AGE (EVENTION AGE)				17
10						
13		IONS AND RECOMMEND Conclusions	ATIONS			<b>19</b> 19
		CONCLUSIONS RECOMMENDATIONS				19 19
	1 <i>3.2</i> P					17



## LIST OF TABLES

- TABLE 2-1
   STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT
- TABLE 3-1
   AIR QUALITY MONITORING STATIONS UNDER THE CONTRACT
- TABLE 3-2
   ENHANCED TSP MONITORING PLAN CONSTRUCTION PHASE
- TABLE 3-3
   ACTION AND LIMIT LEVELS FOR IMPACT AIR QUALITY MONITORING
- TABLE 4-1
   SUMMARY OF AIR QUALITY MONITORING EXCEEDANCE
- TABLE 8-1
   LANDFILL GAS MONITORING ZONE
- TABLE 8-2
   SUMMARY OF LANDFILL GAS MEASUREMENT RESULTS
- TABLE 9-1SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
- TABLE 9-2SUMMARY OF QUANTITIES OF C&D WASTES
- TABLE 10-1
   SITE OBSERVATIONS FOR THE CONTRACT
- TABLE 10-2
   OUTSTANDING ITEMS IN SITE INSPECTION OF PREVIOUS REPORTING PERIOD
- TABLE 11-1
   STATISTICAL SUMMARY OF ENVIRONMENTAL EXCEEDANCE
- TABLE 11-2
   STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
- TABLE 11-3
   STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
- TABLE 11-4
   STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
- TABLE 12-1
   ENVIRONMENTAL MITIGATION MEASURES

## LIST OF APPENDICES

- APPENDIX A PROJECT LAYOUT PLAN
- APPENDIX B LAYOUT PLAN OF THE CONTRACT
- APPENDIX C ORGANIZATION OF THE CONTRACT
- APPENDIX D THREE MONTHS ROLLING PROGRAMME
- APPENDIX E MONITORING LOCATIONS FOR THE CONTRACT
- APPENDIX F EVENT AND ACTION PLAN
- APPENDIX G MONITORING SCHEDULE
- APPENDIX H CALIBRATION CERTIFICATES OF MONITORING EQUIPMENT
- APPENDIX I LANDFILL GAS MONITORING RESULTS AND GRAPHICAL PLOTS
- APPENDIX J INVESTIGATION REPORT FOR EXCEEDANCE
- APPENDIX K CHECKLIST FOR LANDSCAPE AND VISUAL MONITORING
- APPENDIX L MONTHLY SUMMARY WASTE FLOW TABLE
- APPENDIX M ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURES IMPLEMENTATION SCHEDULE (EMIS)
- APPENDIX N CUMULATIVE STATISTICS ON EXCEEDANCE AND COMPLAINT
- APPENDIX O INVESTIGATION REPORT FOR THE COMPLAINT
- APPENDIX P INSPECTION CHECKLIST FOR VULNERABLE TO CONTAMINATED WATER DISCHARGE



## 1 INTRODUCTION

## 1.1 CONTRACT BACKGROUND

- 1.1.1 CRBC-Kaden Joint Venture (hereafter "CRBC-Kaden JV") is commissioned by the Highways Department (HyD) as the Main Contractor of the Contract No. HY/2013/12 Northern Connection Toll Plaza and Tunnel Section ((hereafter "the Contract") and this Contract is part of the Tuen Mun Chek Lap Kok Link (TM-CLK Link Project). TM-CLK Link Project is a Designated Project under Environmental Permit number EP-354/2009/D issued on 13 March 2015. The layout Plan of the Project and the Contract are showed in *Appendix A* and *B* respectively.
- 1.1.2 The construction works of the Contract mainly include:
  - a. construction of an approximately 5.4 hectares toll plaza and an associated footbridge;
  - b. construction of associated carriageways including approximately 0.74 kilometre land viaducts, and an approximately 230 metres vehicular underpass to connect the toll plaza and the roundabout at Lung Mun Road/Lung Fu Road;
  - c. site formation for the construction of the toll plaza, including associated slope works and natural terrain hazard mitigation measures;
  - d. modification and realignment of the existing Lung Mun Road and Lung Fu Road; and
  - e. associated waterworks, drainage, sewerage and landscaping works, etc..
- 1.1.3 This is **28<sup>th</sup>** monthly EM&A report presenting the monitoring results and inspection findings for period from **1 to 28 February 2017**.

## **1.2 REPORT STRUCTURE**

1.2.1 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-

Section 1 Introduction

- Section 2 Contract Organization and Construction Progress and Environmental Submissions
- Section 3 Summary of Impact Monitoring Requirements under the Contract
- Section 4 Air Quality Monitoring
- Section 5 Ecology Monitoring
- Section 6 Cultural Heritage
- Section 7 Landscape and Visual
- Section 8 Landfill gas hazard Monitoring
- Section 9 Waste Management
- Section 10 Inspections and Audit
- Section 11 Environmental Complaints and Non-Compliance
- Section 12 Implementation Status of Mitigation Measures
- Section 13 Conclusions and Recommendations



## 2 CONTRACT ORGANIZATION AND CONSTRUCTION PROGRESS AND ENVIRONMENTAL SUBMISSIONS

## 2.1 CONTRACT ORGANIZATION

2.1.1 The Contract organization and contact details of key personnel are shown in *Appendix C*.

## 2.2 CONSTRUCTION PROGRESS

- 2.2.1 In the Reporting Period, the major construction activity conducted under the Contract is summarized in below. The three-months rolling programme of the Contract is enclosed in *Appendix D*.
  - Instrumentation and Monitoring
  - Site Formation Earthwork on Slope D and E; surface drainage on Slope C, D & E and Portion H;
  - Toll Plaza Decking TD1 and TD2;
  - Toll Plaza Footbridge;
  - Retaining Structure RW\_A, RW\_B and RW\_F;
  - Toll Collector Subway, Toll Booth Canopy & Associated Works;
  - Bridge G1 and Bridge H1 by Form Traveller;
  - Bridge G2
  - Sewer Culvert at FC1 and FC2;
  - Road and Drainage Works at +11mPD, +19mPD, Portion H, Portion J and Lung Mun Road

## 2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.3.1 The environmental submissions under the EP requirement had been submitted to the EPD and they are listed in below:
  - Monitoring Plan on Construction Dust (submission refer to Contract HY/2012/08)
  - Landscape and Visual Plan (not yet endorsed by EPD)
  - Waste Management Plan (endorsed by EPD on 16 March 2015)
  - Baseline Monitoring Report (not yet endorsed by EPD)
- 2.3.2 Summary of environmental permits, licenses and notifications for the Contract is presented in *Table 2-1*.

 Table 2-1
 Status of Environmental Licenses and Permits of the Contract

No.	Type of Permit/ License	Submission Date	Reference/ License No.	Date of Issue	Date of Expiry
1	Air pollution Control (Construction Dust) Regulation	06-08-2014	377719	06-08-2014	N/A
2	Chemical Waste Producer Registration - Waste Producers Number	06-08-2014	5117422C389301	03-09-2014	N/A
3	Water Pollution Control Ordinance -Variation of Effluent Discharge License	22-08-15	WT00023973-2016	14-03-16	30-09-2019
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	21-07-2014	7020460	01-08-2014	N/A
5	CNP for Multiple Task	18-10-2016	GW-RW0619-16	05-11-2016	04-05-2017
6	CNP for MH5	1-11-2016	GW-RW0650-16	18-11-2016	17-05-2017
7	CNP for Tunnel Works	3-11-2016	GW-RW0653-16	23-11-2016	22-05-2017
8	CNP for Falsework Erection	01-12-2016	GW-RW0724-16	28-12-2016	16-03-2017
9	CNP for Portion H Roundabout	21-11-2016	GW-RW0704-16	06-12-2016	21-02-2017
10	CNP for Portion H Roundabout	02-02-2017	GW-RW0049-17	14-02-2017	18-08-2017



# **3 SUMMARY OF IMPACT MONITORING REQUIREMENTS UNDER THE CONTRACT**

## 3.1 GENERAL

- 3.1.1 The major construction activities under the Contract are land-based and no marine work will be involved. In accordance with the Project EM&A Manual requirements, the environmental aspects under the Contract shall be included air quality, ecological, cultural heritage, landscape and visual, landfill gas and site inspection during construction period. In addition, audit of the contractor's implementation of the construction noise and land-based water quality pollution control measures are also required for the Contract.
- 3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

## **3.2 AIR QUALITY MONITORING**

- 3.2.1 The construction phase air quality monitoring shall cover the following parameters:
  - 1-hour TSP; and
  - 24-hour TSP

## 3.3 MONITORING LOCATION

3.3.1 The air quality monitoring stations for impact monitoring are listed in *Table 3-1* and illustrated in *Appendix E*.

ID	Location	Air monitoring station Description			
ASR1	Tuen Mun Fireboat Station	EM&A Manual			
ASR5	Pillar Point Fire Station	EM&A Manual			
AQMS1	Previous River Trade Golf	Enhanced TSP Level under EP condition 2.4			
ASR6	Butterfly Beach Laundry	Enhanced TSP Level under EP condition 2.4			
ASR10	Butterfly Beach Park	Enhanced TSP Level under EP condition 2.4			

 Table 3-1
 Air Quality Monitoring Stations under the Contract

## 3.4 MONITORING FREQUENCY

- 3.4.1 As per Condition 2.4 of the EP of TM-CLKL, an enhanced monitoring plan on TSP level at Tuen Mun ("the Enhanced TSP Monitoring Plan") is required to be submitted to the DEP for approval at least 1 month before the commencement of construction of the Project. Details of the Enhanced TSP Monitoring Plan under Contract No. HY/2012/08 could be found from the project website. The air quality monitoring work under this Contract will follow the monitoring requirement of enhanced TSP monitoring under the project.
- 3.4.2 The air quality monitoring requirements for the Contract is summarized in *Table 3-2*.

Table 3-2Enhanced TSP Monitoring Plan – Construction Phase

Condition	Monitoring Parameter	Monitoring Location	Frequency	Monitoring Requirement
General	1-hour TSP 24-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10 ASR1, ASR5, AQMS1, ASR6, ASR10	3 times per day every six days Daily every six days	Throughout the Northern Connection, toll plaza and tunnel buildings construction works
Special	1-hour TSP 24-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10 ASR1, ASR5, AQMS1, ASR6, ASR10	3 times per day every three days Daily every three days	Northern ConnectionDuring excavation worksforlaunchingshaft,excavation workforcutandCoverConstruction



Condition	Monitoring Parameter	Monitoring Location	Frequency	Monitoring Requirement
				<b><u>Toll Plaza</u></b> During excavation, slope
				works, construction of road
				and superstructures and wind erosion from open
				sites and stockpiling areas
				Tunnel Buildings
				During excavation,
				foundation works,
				construction of
				superstructures and wind
				erosion from open sites and
				stockpiling areas

## 3.5 MONITORING EQUIPMENT

- 3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.*
- 3.5.2 A high volume sampler in compliance with the following specifications shall be used for carrying out the 1-hr and 24-hr TSP monitoring:
  - (i) 0.6-1.7 m3/min (20-60 SCFM) adjustable flow range;
  - (ii) equipped with a timing/control device with +/- 5 minutes accuracy for 24 hours operation;
  - (iii) installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
  - (iv) capable of providing a minimum exposed area of  $406 \text{ cm} 2 (63 \text{ in}^2)$ ;
  - (v) flow control accuracy: +/- 2.5% deviation over 24-hr sampling period;
  - (vi) equipped with a shelter to protect the filter and sampler;
  - (vii) incorporated with an electronic mass flow rate controller or other equivalent devices;
  - (viii) equipped with a flow recorder for continuous monitoring;
  - (ix) provided with a peaked roof inlet;
  - (x) equipped with a manometer;
  - (xi) able to hold and seal the filter paper to the sampler housing in a horizontal position;
  - (xii) easy to change the filter; and
  - (xiii) capable of operating continuously for 24-hr period.
- 3.5.3 Calibration of dust monitoring equipment shall be conducted by the ET upon installation and in bi-monthly intervals during construction phase. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The calibration data shall be properly documented for future reference by concerned parties, such as the IEC. All the data shall be converted into standard temperature and pressure condition.
- 3.5.4 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.
- 3.5.5 If the ET Leader proposes to use a direct reading dust meter to measure 1-hr TSP levels on an ad hoc basis, he shall submit sufficient information to the IEC to prove that the instrument is capable of achieving a comparable result as that the High Volume Sampler (HVS) and may be used for the 1-hr sampling. The instrument should also be calibrated regularly and the 1-hr sampling shall be checked periodically by the HVS to check the validity and accuracy of the results measured by the direct reading method.
- 3.5.6 According to the Project EM&A Manual, wind data monitoring equipment shall also be provided and set up for logging wind speed and wind direction near the dust monitoring



locations. The equipment installation location shall be proposed by the ET Leader and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:

- (i) the wind sensors should be installed on masts at an elevated level 10 m above ground so that they are clear of obstructions or turbulence caused by the buildings;
- (ii) the wind data should be captured by a data logger to be down-loaded for processing at least once a month;
- (iii) the wind data monitoring equipment should be re-calibrated at least once every six months; and
- (iv) wind direction should be divided into 16 sectors of 22.5 degrees each.

## 3.6 DERIVATION OF ACTION/LIMIT (A/L) LEVELS

3.6.1 The baseline monitoring results formed the basis for determining the air quality criteria for the impact monitoring. The ET shall compare the impact monitoring results with air quality criteria set up for 24-hour TSP and 1-hour TSP. Based on results of the approved Baseline Monitoring Report of HyD Contract HY/2012/08, the Action and Limit Levels for impact dust monitoring are shown in *Tables 3-3*.

Air Quality Monitoring	24-hour TSP (μg/m <sup>3</sup> )		1-hour TSP (μg/m <sup>3</sup> )		
Stations	Action Level	Limit Level	Action Level	Limit Level	
ASR1	213	260	331	500	
ASR5	238	260	340	500	
AQMS1	213	260	335	500	
ASR6	238	260	338	500	
ASR10	214	260	337	500	

 Table 3-3
 Action and Limit Levels for Impact Air Quality Monitoring

3.6.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in *Appendix F*.

## 3.7 OTHER ENVIRONMENTAL ASPECTS

## <u>Noise</u>

- 3.7.1 The TM-CLKL EIA study stated that no existing noise sensitive receiver (NSR) was identified within the Study Area at Tuen Mun. Therefore, no noise monitoring is required for the construction phase of the Contract.
- 3.7.2 Regular site inspections and audits will be carried out during the construction phase in order to confirm the construction works under the Contract comply with the regulatory noise requirements.

## Water Quality

3.7.3 No marine works will be undertaken under the Contract. Therefore, no water quality monitoring is required for the construction phase of the Contract.

## <u>Ecology</u>

- 3.7.4 No marine works will be undertaken under the Contract and generated marine ecological impact, no dolphin monitoring is required for the construction phase of the Contract.
- 3.7.5 During construction phase, the ET will perform Pitcher Plants inspection at least once every week to report the growth condition (only undertaken at Establishment period) and protection measures.

## Landscape and Visual

3.7.6 Measures to mitigate landscape and visual impact during construction should be checked and



monitored by a Registered Landscape Architect to ensure compliance with the intended aims of the mitigation measures in accordance with the EM&A Manual.

## <u>Cultural Heritage</u>

3.7.7 Grave G1 as a heritage resource is situated near the proposed toll plaza in Tuen Mun. Site inspections should be undertaken at least once per week throughout the construction period to ensure compliance with the intended aims of recommended mitigation measures.

## Landfill Gas

3.7.8 During EIA study, landfill gas hazards are likely to be generated from the Pillar Point Valley (PPV) Landfill. Landfill gas monitoring is recommended during construction of the Contract to ensure the works area is free of landfill gas before the worker entered the concerned area.

## 3.8 MONITORING SCHEDULE

3.8.1 The monitoring schedule for landscape &visual and landfill gas for the present and next reporting period are presented in *Appendix G*.



## 4 AIR QUALITY MONITORING

## 4.1 GENERAL

4.1.1 The air quality impact monitoring and enhanced Total Suspended Particulates (TSP) level monitoring at five proposed locations are currently carried out by the ET of Contract HY/2012/08. Sharing of impact air quality monitoring data between HY/2012/08 and HY/2013/12 is agreed by all relevant parties. The Contract is not required to conduct its own dust monitoring exercise until the Contract HY/2012/08 ends.

## 4.2 AIR QUALITY MONITORING RESULTS IN REPORTING PERIOD

4.2.1 In the Reporting Period, 1-hour and 24-hour TSP monitoring at the five proposed locations are continued to perform by the ET of Contract HY/2012/08. Therefore, no air quality monitoring was conducted by the ET of Contract HY/2013/12. Details information of air quality monitoring results could be referred to the Monthly EM&A Reports of the Contract HY/2012/08 (February 2017).

## 4.3 ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE

4.3.1 According to the air quality monitoring result provided by Contract HY/2012/08, no exceedances in 1-hour and 24-hour TSP were recorded in the Reporting Period. No Notification on Exceedances (NOEs) was issued by the ET of Contract HY/2012/08. The summary of air quality exceedance in the Reporting Period is shown in *Table 4-1*.

## Table 4-1Summary of Air Quality Monitoring Exceedance

Date of Exceedance	Monitoring Station	Air Quality Parameter	Result	Exceed
NA	NA	NA		

## 4.4 AIR QUALITY EXCEEDANCE INVESTIGATION

4.4.1 No investigation for exceedance is required for the Reporting Period.



## 5 ECOLOGY MONITORING

## 5.1 GENERAL

- 5.1.1 According to the EM&A Manual requirements, regularly inspection for Pitcher Plants shall be conducted at least once every week to report the protection measure of the Pitcher Plants during construction period.
- 5.1.2 A total of 181 pitcher plants were transplanted to final receptor site and the rest of the Pitcher Plant individuals (certified dead by the specialist) were not transplanted and were treated as general refuse. All the transplantation of pitcher plant from the nursery site to final receptor site was completed on 10<sup>th</sup> September 2015.

## 5.2 PITCHER PLANTS INSPECTION

- 5.2.1 Inspection for the mitigation measures implementation status of the Pitcher Plant at the final receptor area were performed on 2<sup>nd</sup>, 7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> February 2017 by the ET in the Reporting Period.
- 5.2.2 Establishment period for the pitcher plants was completed at the end of September 2016, the join site completion of Establishment period visit with AFCD was undertaken on 23 September 2016 and the final pitcher plants report was submitted to AFCD on early December 2016. Therefore after 23 September 2016, only the integrity of the protection fence was checked to fulfil the EIA requirement. During each inspection, the protection mitigation measures were checking at the final receptor area to make sure no site activities was undertaken inside the protection zone. Besides, no construction activities were observed to be carried out at the surrounding of the final receptor area. The condition of chain link fence is good and no repair or maintenance is required.
- 5.2.3 No matters the completion of Establishment period, the Contractor should properly maintain the fencing along the receptor area to avoid disturbance to the pitcher plants under the EIA requirement.



## 6 CULTURAL HERITAGE

## 6.1 GENERAL

- 6.1.1 According to the EM&A Manual requirements, regular inspection for heritage resource, Grave G1, shall be audited by the ET at least once every week to ensure recommended mitigation measures implemented during construction period. The aim of the survey is to prevent any possible damage to the grave and to ensure the proposed mitigation measures are implemented. The broad scope of the audit will involve supervision of the following:
  - Non-contact effects of the engineering works, such as vibration from pneumatic drills which could cause damage, such as foundation or wall cracks and loosening of tiles or fixtures; and
  - Contact between the historic structures and equipment and materials associated with the engineering works.
- 6.1.2 Specifically, the monitoring programme will entail the following tasks:
  - The extent of the agreed works areas should be regularly checked during the construction phase to ensure the buffer is being maintained; and
  - Ensure no stockpiling or equipment storage is affecting the structure.
- 6.1.3 In the event of non-compliance the responsibilities of the relevant parties is detailed in the Event/ Action Plan in *Appendix F*.

## 6.2 **GRAVE INSPECTION**

- 6.2.1 In the Reporting Period, Grave G1 of inspection was undertaken on 2<sup>nd</sup>, 7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> February 2017. During these inspections, buffer zone was maintained between the working area and the Grave. The nearby areas were clean, and no construction materials or mechanical equipment were stored within or close to the buffer zone. Moreover protective measures (hoarding and scaffold with protective net above the grave) was provided for constructing Toll Plaza Decking TD2 deck structure.
- 6.2.2 Since construction works very close to buffer zone of the Grave G1, cultural heritage mitigation measures and protection measures as provided by the Contractor, therefore has fully implemented in accordance with EM&A Manual requirements.



## 7 LANDSCAPE AND VISUAL

## 7.1 GENERAL

7.1.1 According to EM&A Manual requirements, monitoring of Contractor's operations during construction period to report on Contractor's compliance should be carried out on weekly basis. Measure to mitigate landscape and visual impact during construction should be checked and monitored by a Registered Landscape Architect to ensure compliance with the intended aims of the mitigation measures. Moreover, the progress of the engineering works shall be regularly reviewed on site to identify the earliest practical opportunities for the landscape works to be undertaken.

## 7.2 LANDSCAPE AND VISUAL INSPECTION

- 7.2.1 In the Reporting Period, site inspection for landscape and visual mitigation measures was undertaken on 3<sup>rd</sup>, 10<sup>th</sup>, 17<sup>th</sup> and 24<sup>th</sup> February 2017 by the Registered Landscape Architect.
- 7.2.2 Most of the landscape works such as planting was not yet commenced. The detailed inspection checklists were provided in *Appendix K*.



## 8 LANDFILL GAS HAZARD MONITORING

## 8.1 GENERAL

- 8.1.1 During EIA study, landfill gas hazards are likely to be generated from the Pillar Point Valley (PPV) Landfill. Hence, regular landfill gas monitoring is recommended during construction of the proposed toll plaza.
- 8.1.2 During construction, a Safety Officer should be appointed to carry out the monitoring works. The monitoring frequency and areas to be monitored should be set down prior to commencement of ground-works either by the Safety Officer or an approved and appropriated qualified person. The routine monitoring should be carried out in all excavations, manholes, chambers, relocation of monitoring wells and any other confined spaces that may have been created. All measurements in excavations should be made with the extended monitoring tube located not more than 10 mm from the exposed ground surface. Monitoring should be performed properly to make sure that the area is free of landfill gas before any man enters in the area.
- 8.1.3 For excavations deeper than 1m, measurements should be carried out:
  - at the ground surface before excavation commences;
  - immediately before any worker enters the excavation;
  - at the beginning of each working day for the entire period the excavation remains open; and
  - periodically through the working day whilst workers are in the excavation.
- 8.1.4 For excavations between 300mm and 1m deep, measurements should be carried out:
  - directly after the excavation has been completed; and
  - periodically whilst the excavation remains open
- 8.1.5 For excavations less than 300mm deep, monitoring may be omitted, at the discretion of the Safety Officer (SO) or other appropriately qualified person.
- 8.1.6 To ensure the accuracy of the monitoring data, zeroing of the gas analyser shall be undertaken at the start of each day's monitoring. As advised by the SO, the gas analyser would be optimally calibrated by the self-test function to provide the most accurate result. The gas analyser is calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.
- 8.1.7 The landfill consultation zone was divided into 6 monitoring zones. The landfill gas monitoring zones are summarized in *Table 8-1* and the layout plan for the monitoring zone is illustrated in *Appendix E*.

ID	Location	Excavation >300mm deep undertaken in this reporting period
TD1	TD1, Retaining Wall A, Grave G1 and	Yes
	Subway	
RW-B	Retaining Wall B	No
RW-F	Retaining Wall F	No
S&U	Slope and Underpass	No
BW	Bridge Works (G2, H1)	No
LMR	Lung Mun Road	Yes

Table 8-1Landfill Gas Monitoring Zone

## 8.2 LANDFILL GAS MONITORING RESULT

8.2.1 In the Reporting Period, landfill gas monitoring was conducted at the zone TD1 and LMR



which have excavation works was undertaking. A BIOGAS 5000 gas analyser was used for the landfill gas monitoring and the valid calibration certificate is presented in *Appendix H*.

8.2.2 There were a total of **24** days monitoring were carried by the Safety Officer or an approved and qualified persons. The results of landfill gas measurement are summarized in *Table 8-2*. Moreover, database of monitoring result and graphical plot are attached in *Appendix I*.

Landfill Gas Action		Limit	Detectab	le at TD1	Detectable at LMR	
Parameter	Level	Level	Min	Max	Min	Max
Methane	>10% LEL (>0.5% v/v)	>20% LEL (>1% v/v)	0.1%	0.1%	0.1%	0.1%
Oxygen	<19%	<18%	21.0%	21.1%	21.0%	21.1%
Carbon Dioxide	>0.5%	>1.5%	0.1%	0.2%	0.1%	0.2%

 Table 8-2
 Summary of Landfill Gas Measurement Results

8.2.3 The measurement results shown that slightly methane concentration was detected and oxygen concentration measured was over 21.0 % and Carbon Dioxide was between 0.1% and 0.2 %. No exceedance was triggered and therefore no corrective action was required accordingly.



## 9 WASTE MANAGEMENT

### 9.1 GENERAL WASTE MANAGEMENT

- 9.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time. The effective management of waste arising during the construction phase will be monitored through the site audit programme. The aims of the waste audit are:
  - to ensure the waste arising from the works are handled, stored, collected, transferred and disposed of in an environmentally acceptable manner; and
  - to encourage the reuse and recycling of material.
- 9.1.2 In addition to the site inspections, the ET shall review the documentation procedures prepared by the Waste Coordinator once a week to ensure proper records are being maintained and procedures undertaken in accordance with the Waste Management Plan.

## 9.2 **RECORDS OF WASTE QUANTITIES**

- 9.2.1 All types of waste arising from the construction work are classified into the following:
  - Construction & Demolition (C&D) Material;
  - Chemical Waste;
  - General Refuse; and
  - Excavated Soil.
- 9.2.2 The quantities of wastes generated under the Contract in this Reporting Period are summarized in *Tables 9-1* and *9-2* and the Monthly Summary Waste Flow Table is shown in *Appendix L*. Whenever possible, materials were reused on-site as far as practicable.

Table 9-1Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	<b>Disposal Location</b>
Reused in this Contract (Inert) (`000m <sup>3</sup> )	1.066	-
		1. Lam Tei Quarry
		2. Eco Park K.Wah Recycle
		Facilities
		3. Lung Kwu Tan Tailor Recycled
Reused in other Projects (Inert) (`000m <sup>3</sup> )	10.617	Aggregates
		4. Liantang BCP Project
		5. TM-CLKL Contract 2 -
		Northern Connection Sub-sea
		Tunnel Section Project
Disposal as Public Fill (Inert) (`000m <sup>3</sup> )	2.566	Tuen Mum Area 38

## Table 9-2Summary of Quantities of C&D Wastes

Type of Waste	Quantity	<b>Disposal Location</b>
Recycled Metal (`000kg)	0	-
Recycled Paper / Cardboard Packaging (`000kg)	0	-
Recycled Plastic (`000kg)	0	-
Chemical Wastes (`000kg)	0	License Collector
General Refuses (`000m <sup>3</sup> )	0.074	WENT



## 10 INSPECTION AND AUDIT

## **10.1** SITE INSPECTION

10.1.1 According to the approved EM&A Manual, the environmental site inspection shall be formulated by ET Leader on weekly basis to confirm the environmental performance of the construction site.

## Findings / Deficiencies During Reporting Period

- 10.1.2 In the Reporting Period, joint site inspections to evaluate site environmental performance were carried out by the RE, ET and the Contractor on 2<sup>nd</sup>, 7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> February 2017. No non-compliance was noted but 1 observation and 4 reminders were recorded during site inspection. Moreover, ENPO/IEC has attended joint site inspection on 28<sup>th</sup> February 2017.
- 10.1.3 The findings / deficiencies observed during the weekly site inspection in the Reporting Period are listed in *Table 10-1*.

<b>I</b>		
Date	Findings / Deficiencies	Follow-Up Status
2 February 2017	• Empty bucket cumulated on site should be cleaned. (Retaining Wall A)	• Not required for reminder.
7 February 2017	• Stockpile storage on site should be covered to minimize dust generation (Central Divider)	• Not required for reminder.
14 February 2017	• Broken tarpaulin covered on the exposed slope should be replaced. (Bridge H1)	• Broken tarpaulin was replaced.
21 February 2017	• Dust control measures frequency should be increased during dry season to minimize dust impact. (General)	• Not required for reminder.
28 February 2017	• Proper dust mitigation measures should be provided for stockpile on site to minimize dust impact. (Retaining Wall F)	• Not required for reminder.

 Table 10-1
 Site Observations for the Contract

10.1.4 No outstanding deficiency remained to be rectified in previous Reporting Period which presented in *Table 10-2*.

<b>Table 10-2</b>	Outstanding Items in	n Site Inspection o	of previous Reporting Period
-------------------	----------------------	---------------------	------------------------------

Date	Findings / Deficiencies	Follow-Up Status	
	• NA	• NA	

- 10.1.5 Air quality mitigation measures such as watering of site area for 12 times per day and covering of exposed slopes should be implemented during the construction period to reduce construction dust impact as recommended in the EMIS.
- 10.1.6 Good site practice for daily housekeeping is reminded. In addition, clean-up of the waste skips and wastewater treatment system should be increased to ensure these facilities functional and effective.
- 10.1.7 In addition, muddy water or other water pollutants from site surface runoff shall not be discharged into public areas. Water quality mitigation measures to prevent surface runoff into the public areas should be paid on special attention.



10.1.8 Stagnant water should be removed as soon as possible after rain to prevent mosquito breeding on site.

## Inspection Checklist for Vulnerable to Contaminated Water Discharge

- 10.1.9 Following to the complaint about discharge of milky water to Bufferfuly Beach on 2 September 2015. The Contractor proposed to carry out daily inspection of wastewater treatment facilities, concerned discharge points, drainage inlets and outlets during typhoon or wet season.
- 10.1.10 In addition, specific inspections would also be conducted before and after adverse weather to ensure necessary remedial works would be carried out timely. Should incidental contaminated water discharge be found at the inlet of the associated drainage system, a specific inspection of the relevant drainage pipes would be conducted for traces of deposit, and follow up actions would be taken when necessary.
- 10.1.11 The daily inpsection for vulnerable to contaminated water discharge was temporarily suspended during the dry season and will be resumed at wet season or after the rainstorm warnings. As requested by the EPD, the associated inspection checklist should be presented in the Monthly EM&A Report and it is shown in *Appendix P* (if necessary).



## 11 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

### 11.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

- 11.1.1 In the Reporting Period, no environmental complaint, summons and prosecution under the EM&A Programme was lodged. Moreover, no exceedance of the environmental performance (Action / Limit Levels) was recorded for monitoring programme.
- 11.1.2 The statistical summary table of environmental exceedance, complaint, summons and prosecution are presented in *Tables 11-1, 11-2, 11-3 and 11-4*.

Reporting	Environmental	Environmental	Eve	ent Exceedan	ce
Period	Aspect / Parameter	Performance	Reporting Month	Previous Months	Cumulative
	Air Quality -	Action Level	0	4	4
February	1-hr TSP	Limit Level	0	0	0
2017	Air Quality -	Action Level	0	0	0
	24-hr TSP	Limit Level	0	0	0

 Table 11-1
 Statistical Summary of Environmental Exceedance

Table 11-2	<b>Statistical Summar</b>	v of Environmental	Complaints
	Statistical Summar	J OI LIN II OIIIIIOIIOM	Complaints

	Environmental Complaint Statistics				
<b>Reporting Period</b>	Encourance	Cumulativa	Complaint Nature		
	Frequency	Cumulative	Air	Noise	Water
February 2017	0	7	1	NA	6

## Table 11-3 Statistical Summary of Environmental Summons

		Environme	ental Summon	s Statistics	
<b>Reporting Period</b>	Engenerati	Cumulativa	Co	omplaint Natu	re
	Frequency	Cumulative	Air	Noise	Water
February 2017	0	0	NA	NA	NA

## Table 11-4 Statistical Summary of Environmental Prosecution

	Environmental Prosecution Statistics				
<b>Reporting Period</b>	Frequency	Cumulativa	Co	omplaint Natu	re
	rrequency	Cumulative	Air	Noise	Water
February 2017	0	0	NA	NA	NA

11.1.3 In the Reporting Period, no warning letter related to environmental issue was received from the EPD or HyD.



## 12 IMPLEMENTATION STATUS OF MITIGATION MEASURES

## **12.1** GENERAL REQUIREMENTS

- 12.1.1 The environmental mitigation measures that recommended in the Environmental Mitigation and Enhancement Measures Implementation Schedule (EMIS) for in the Project EM&A Manual covered the issues of air quality, cultural heritage, ecology, landfill gas hazard, landscape & visual, noise, water and waste. The updated EMIS for the Contract is shown in *Appendix M*.
- 12.1.2 The Contractor shall implement the required environmental mitigation measures according to the EM&A Manual as subject to the site condition. The environmental mitigation measures implemented by the Contract in this Reporting Period are summarized in *Table 12-1* and *Appendix M*.

Issues	Environmental Mitigation Measures
Air Quality	Maintain damp / wet surface on access road
-	• Keep slow speed in the sites
	All vehicles must use wheel washing facility before off site
	Sprayed water during rock breaking works
	• During transportation by truck, materials loaded lower than the side and tail
	boards, and covered before transport
	Compacted all soil stockpiles
	<ul> <li>Part of the exposed slopes covered geotextile net</li> </ul>
Cultural	• Set a buffer zone between the working area and the Grave
Heritage	All construction materials and equipment store far from the Grave
	Inspection the Grave to ensure provision mitigation measures effective
Ecology	<ul> <li>Wire fencing provided for temporary protect Pitcher Plants</li> </ul>
	Undertake weekly inspection of Pitcher Plants
Landfill Gas	Landfill Gas measurement undertake during trench excavation
Hazard	
Water	• Temporary drainage system provide for surface runoff prevent discharge to
Quality	public area
	<ul> <li>Wastewater to be treated by sedimentation tank before discharge.</li> </ul>
Noise	• Restrain operation time of plants from 07:00 to 19:00 on any working day
	except for Public Holiday and Sunday.
	Keep good maintenance of plants
	<ul> <li>The noisy plants or works provide mobile noise barriers</li> </ul>
	Shut down the plants when not in used
Waste and	On-site sorting prior to disposal
Chemical	<ul> <li>Follow requirements and procedures of the "Trip-ticket System"</li> </ul>
Management	Predict required quantity of concrete accurately
	· Collect the unused fresh concrete at designated locations in the sites for
	subsequent disposal
General	• The site was generally kept tidy and clean.

Table 12-1Environmental Mitigation Measures

## **12.2** TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

12.2.1 Construction activities as undertaken in the coming month for the Contract lists below:

- Site Formation Earthwork on Slope D and E; surface drainage on Slope C, D & E and Portion H;
  - Toll Plaza Decking TD1 and TD2;
  - Toll Plaza Footbridge;
  - Retaining Structure RW\_A, RW\_B and RW\_F;
  - Toll Collector Subway & Associated Works;
  - Bridge G1, G2 and Bridge H1 by Form Traveller;
  - Sewer Culvert at FC1 and FC2;
  - Waterproofing and lining at Vehicular Underpass; and



• Road and Drainage Works at +11mPD, +19mPD and Portion H

## 12.3 KEY ENVIRONMENTAL ISSUES FOR THE COMING MONTH

- 12.3.1 Key environmental issues to be considered in the coming month include:
  - Implementation of dust suppression measures at all times;
  - Potential wastewater quality impact due to surface runoff;
  - Potential fugitive dust impact due to the dry/loose/exposure soil surface/dusty material;
  - Ensure dust suppression measures are implemented properly;
  - Sediment catch-pits and silt removal facilities should be regularly maintained;
  - Management of chemical wastes;
  - Site effluent discharge to the nearby nullah is prohibited;
  - Follow-up of improvement on general waste management issues; and
  - Implementation of construction noise preventative control measures



## 13 CONCLUSIONS AND RECOMMENDATIONS

## 13.1 CONCLUSIONS

- 13.1.1 This is **28**<sup>th</sup> monthly EM&A report presenting the monitoring results and inspection findings for the period of **1**<sup>st</sup> to **28**<sup>th</sup> February 2017.
- 13.1.2 No air quality monitoring including 1-hour and 24-hour TSP exceedance was recorded in the Reporting Period.
- 13.1.3 In the Reporting Period, no noise complaint was received by RE, the Contractor, ENPO or HyD. No Action Level exceedances were therefore triggered and no NOE or the associated corrective actions were required.
- 13.1.4 Site inspection for landscape and visual was conducted on weekly basis by the Landscape Architect to ensure the compliance of the intended aims of the mitigation measures. Most of the landscape works such as planting was not yet commenced.
- 13.1.5 Establishment period for the pitcher plants was completed at the end of September 2016, the join site completion of Establishment period visit with AFCD was undertaken on 23 September 2016 and the final pitcher plants report was submitted to AFCD on early December 2016. Therefore after 23 September 2016, only the integrity of the protection fence was checked to fulfil the EIA requirement. During each inspection, the protection mitigation measures were checking at the final receptor area to make sure no site activities was undertaken inside the protection zone. Besides, no construction activities were observed to be carried out at the surrounding of the final receptor area. The condition of chain link fence is good and no repair or maintenance is required.
- 13.1.6 Landfill gas monitoring was conducted at the TD1 and Lung Mun Road works area. The monitoring results shown no exceedances were triggered.
- 13.1.7 In the Reporting Period, no environmental complaint was received.
- 13.1.8 No notifications of summons, or successful prosecution were received by the Contractor during the Reporting Period.
- 13.1.9 In the Reporting Period, joint site inspection by the RE, ET and the Contractor was carried out on 2<sup>nd</sup>, 7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> February 2017 and the IEC has attended the joint site inspection on 28<sup>th</sup> February 2017. No non-compliance was recorded during the site inspection but 1 observation and 4 reminders were recorded.
- 13.1.10 In the Reporting Period, Grave G1 of inspection was undertaken on 2<sup>nd</sup>, 7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> February 2017. Based on the inspection findings, the cultural heritage mitigation measures as implemented by the Contractor are fully complied with the EM&A Manual requirements.

## **13.2 RECOMMENDATIONS**


- 13.2.1 During dry season, air quality mitigation measures such as watering of site area for 12 times per day and covering of exposed slopes should be fully implemented to reduce construction dust impact as recommended in the EMIS.
- 13.2.2 Moreover, muddy water or other water pollutants from site surface runoff into the public areas will be key environment issue. Special attention should be paid on the water quality mitigation measures to prevent surface runoff flow to public area.
- 13.2.3 Stagnant water should be removed as soon as possible after rain to prevent mosquito breeding on site.



Appendix A

## **Project Layout Plan**


 $Z:\label{eq:loss_2014} CS00715(HY-2013_{12})\label{eq:loss_2014} Monthly EM&A Report \label{eq:loss_2017} Pebruary \label{eq:loss_2014} 2017\end{tabular} R0278v2.docx$ 

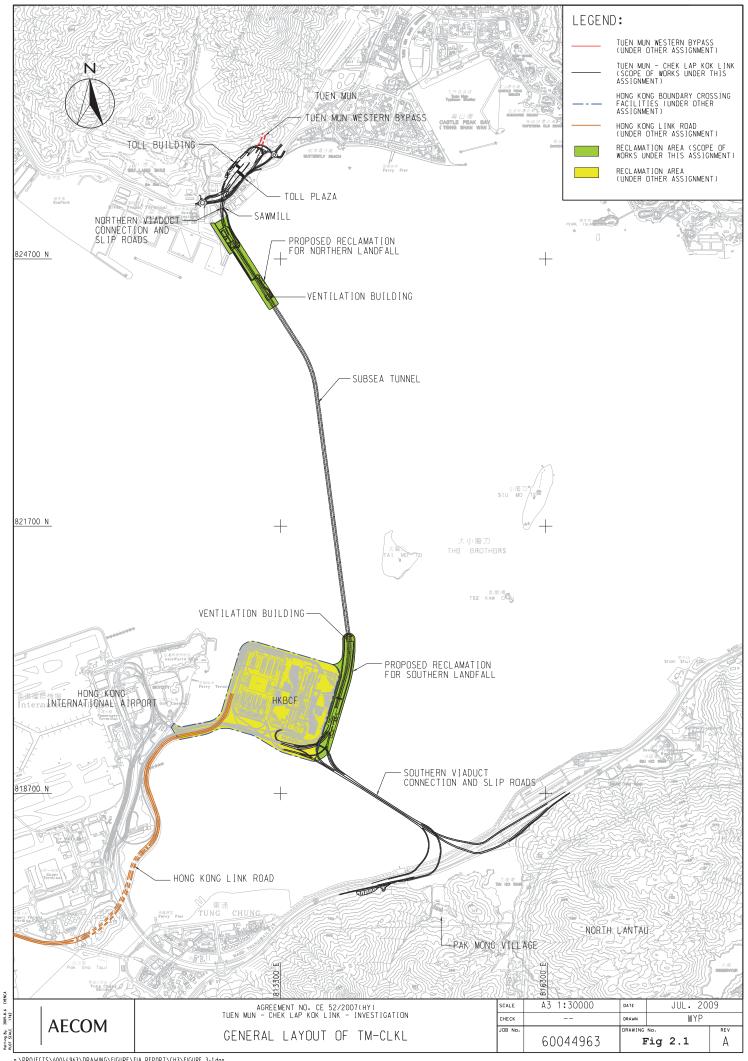




# Appendix B

## Layout Plan of the Contract

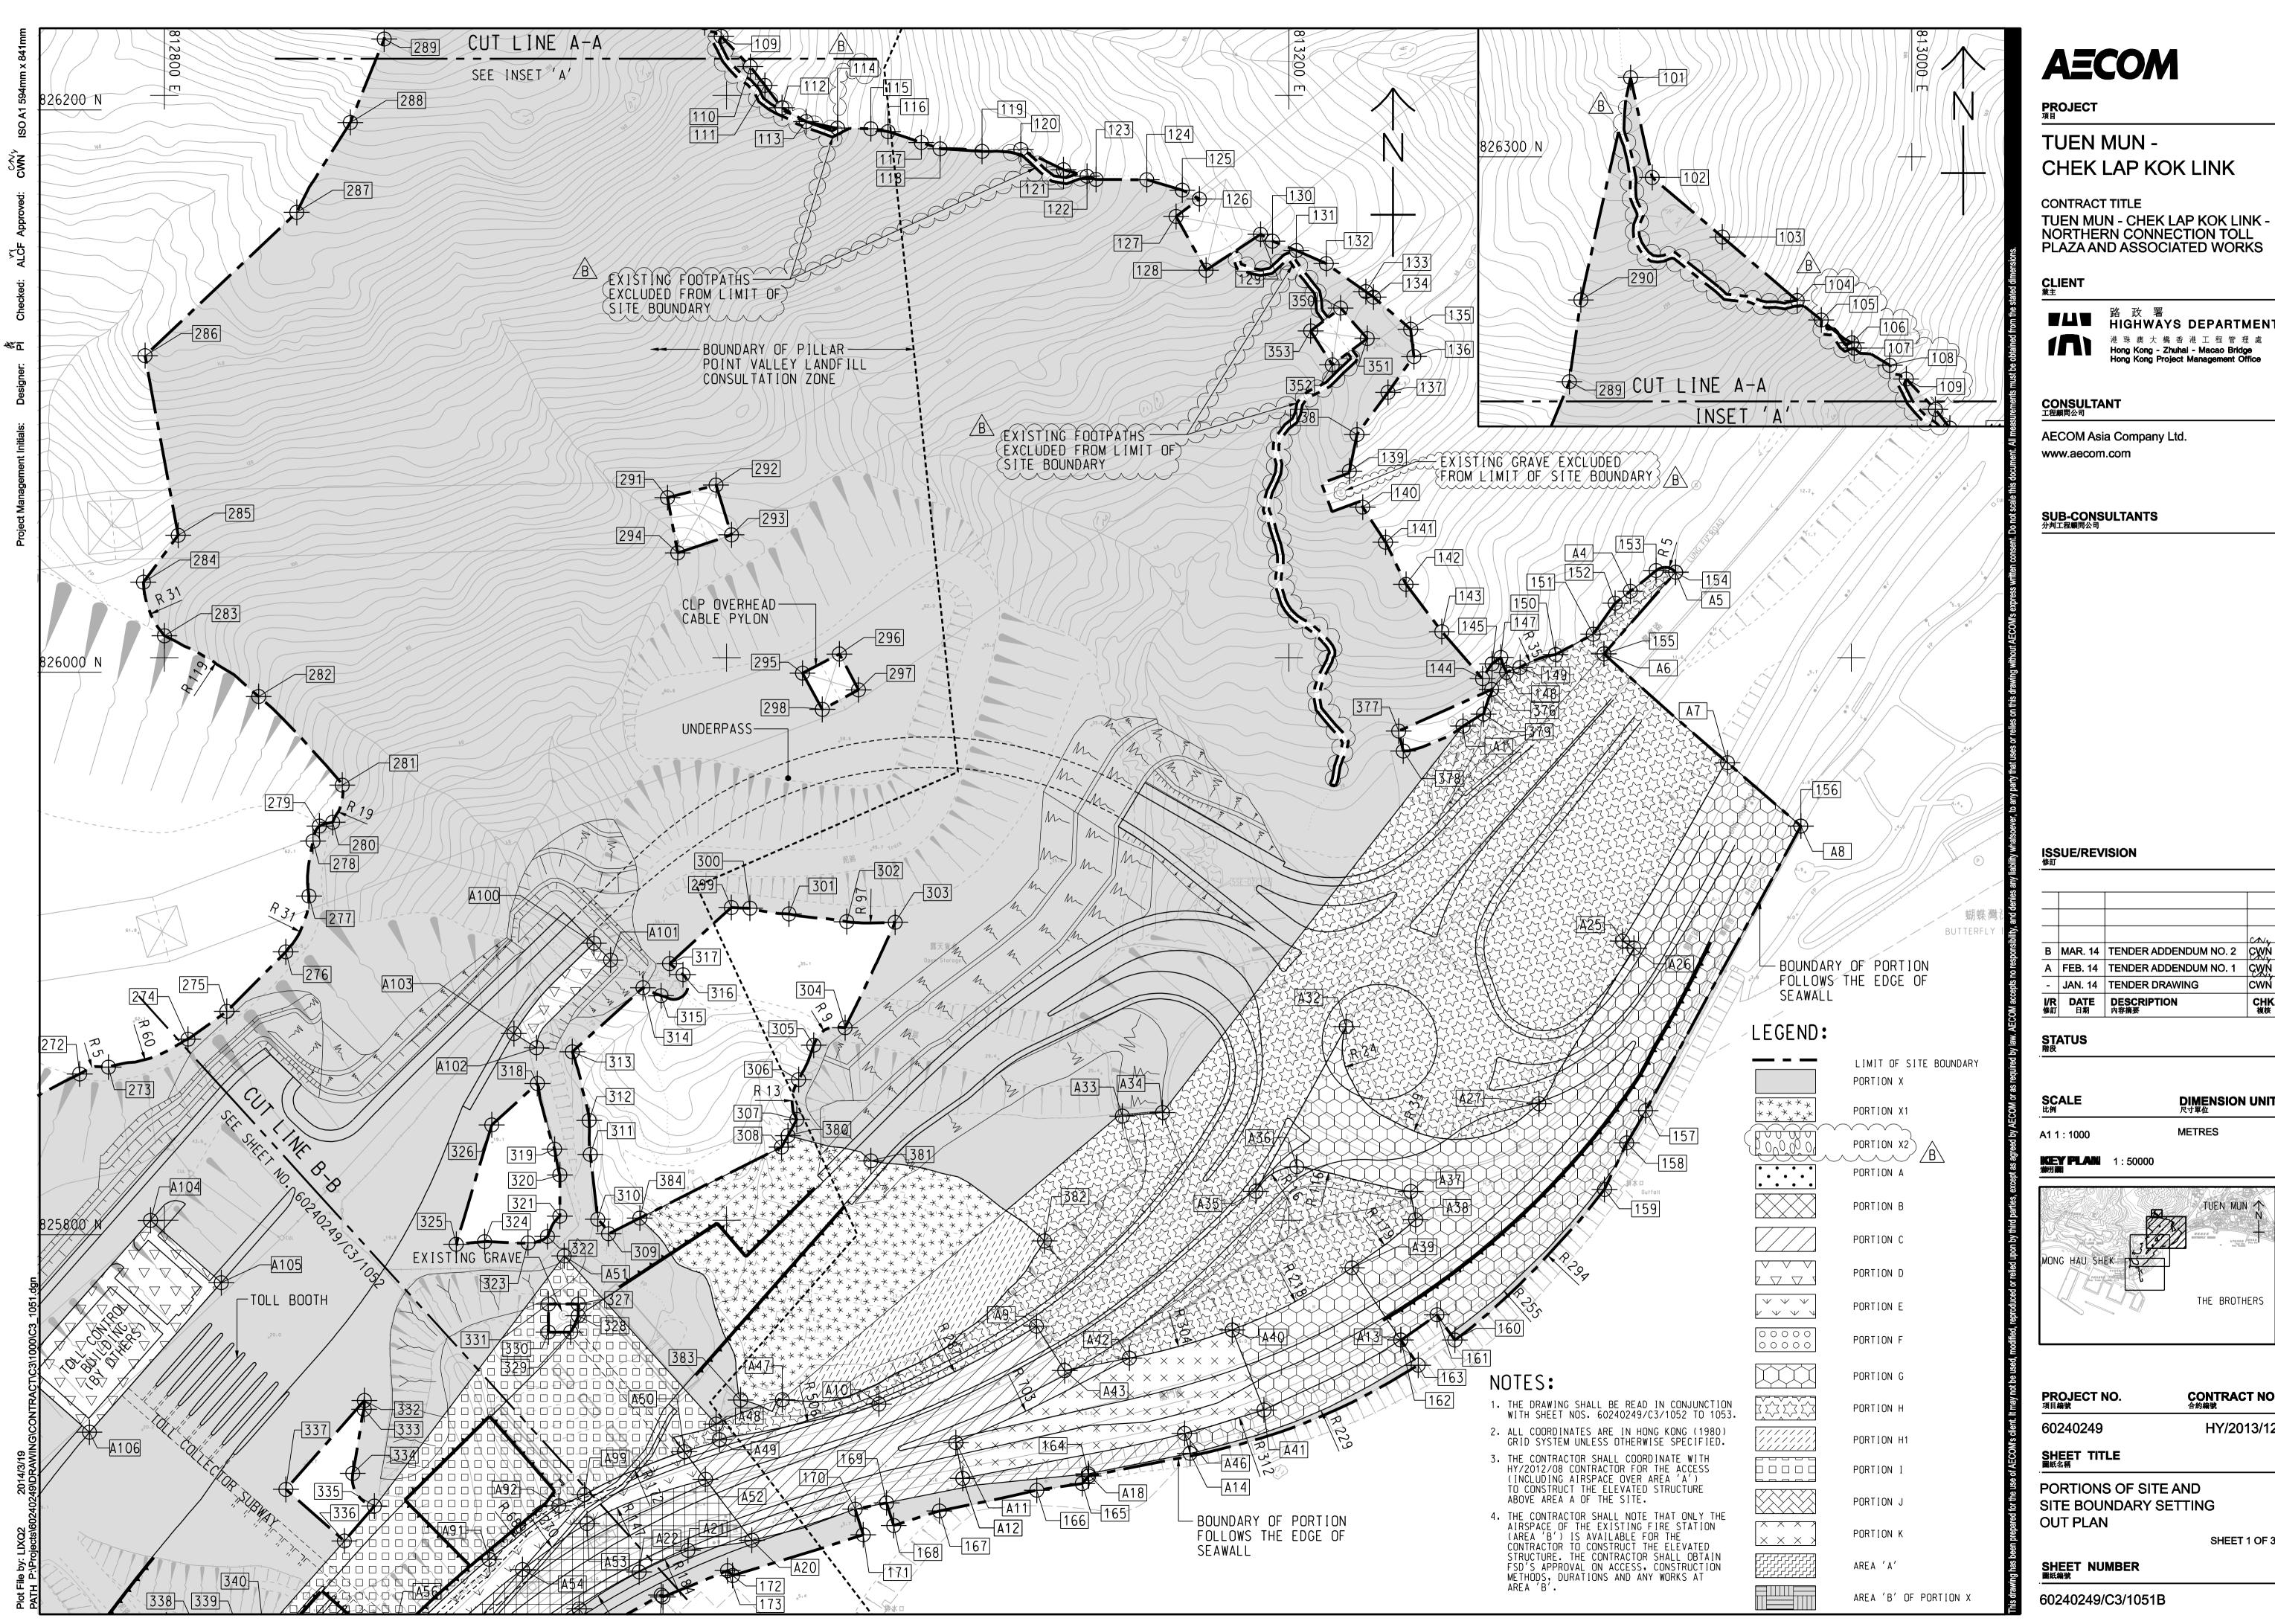



# CONTRACT NO. <sup>合約編</sup>號

HY/2013/12

SHEET 1 OF 3


DIMENSION UNIT <sup>尺寸單位</sup>

TUEN MUN

THE BROTHERS

METRES






# SUB-CONSULTANTS 分判工程順間公司


■▲■ <sup>路</sup>政署 HIGHWAYS DEPARTMENT

AECOM Asia Company Ltd.

港 珠 傸 大 橋 香 港 工 程 管 理 處 Hong Kong - Zhuhai - Macao Bridge Hong Kong Project Management Office





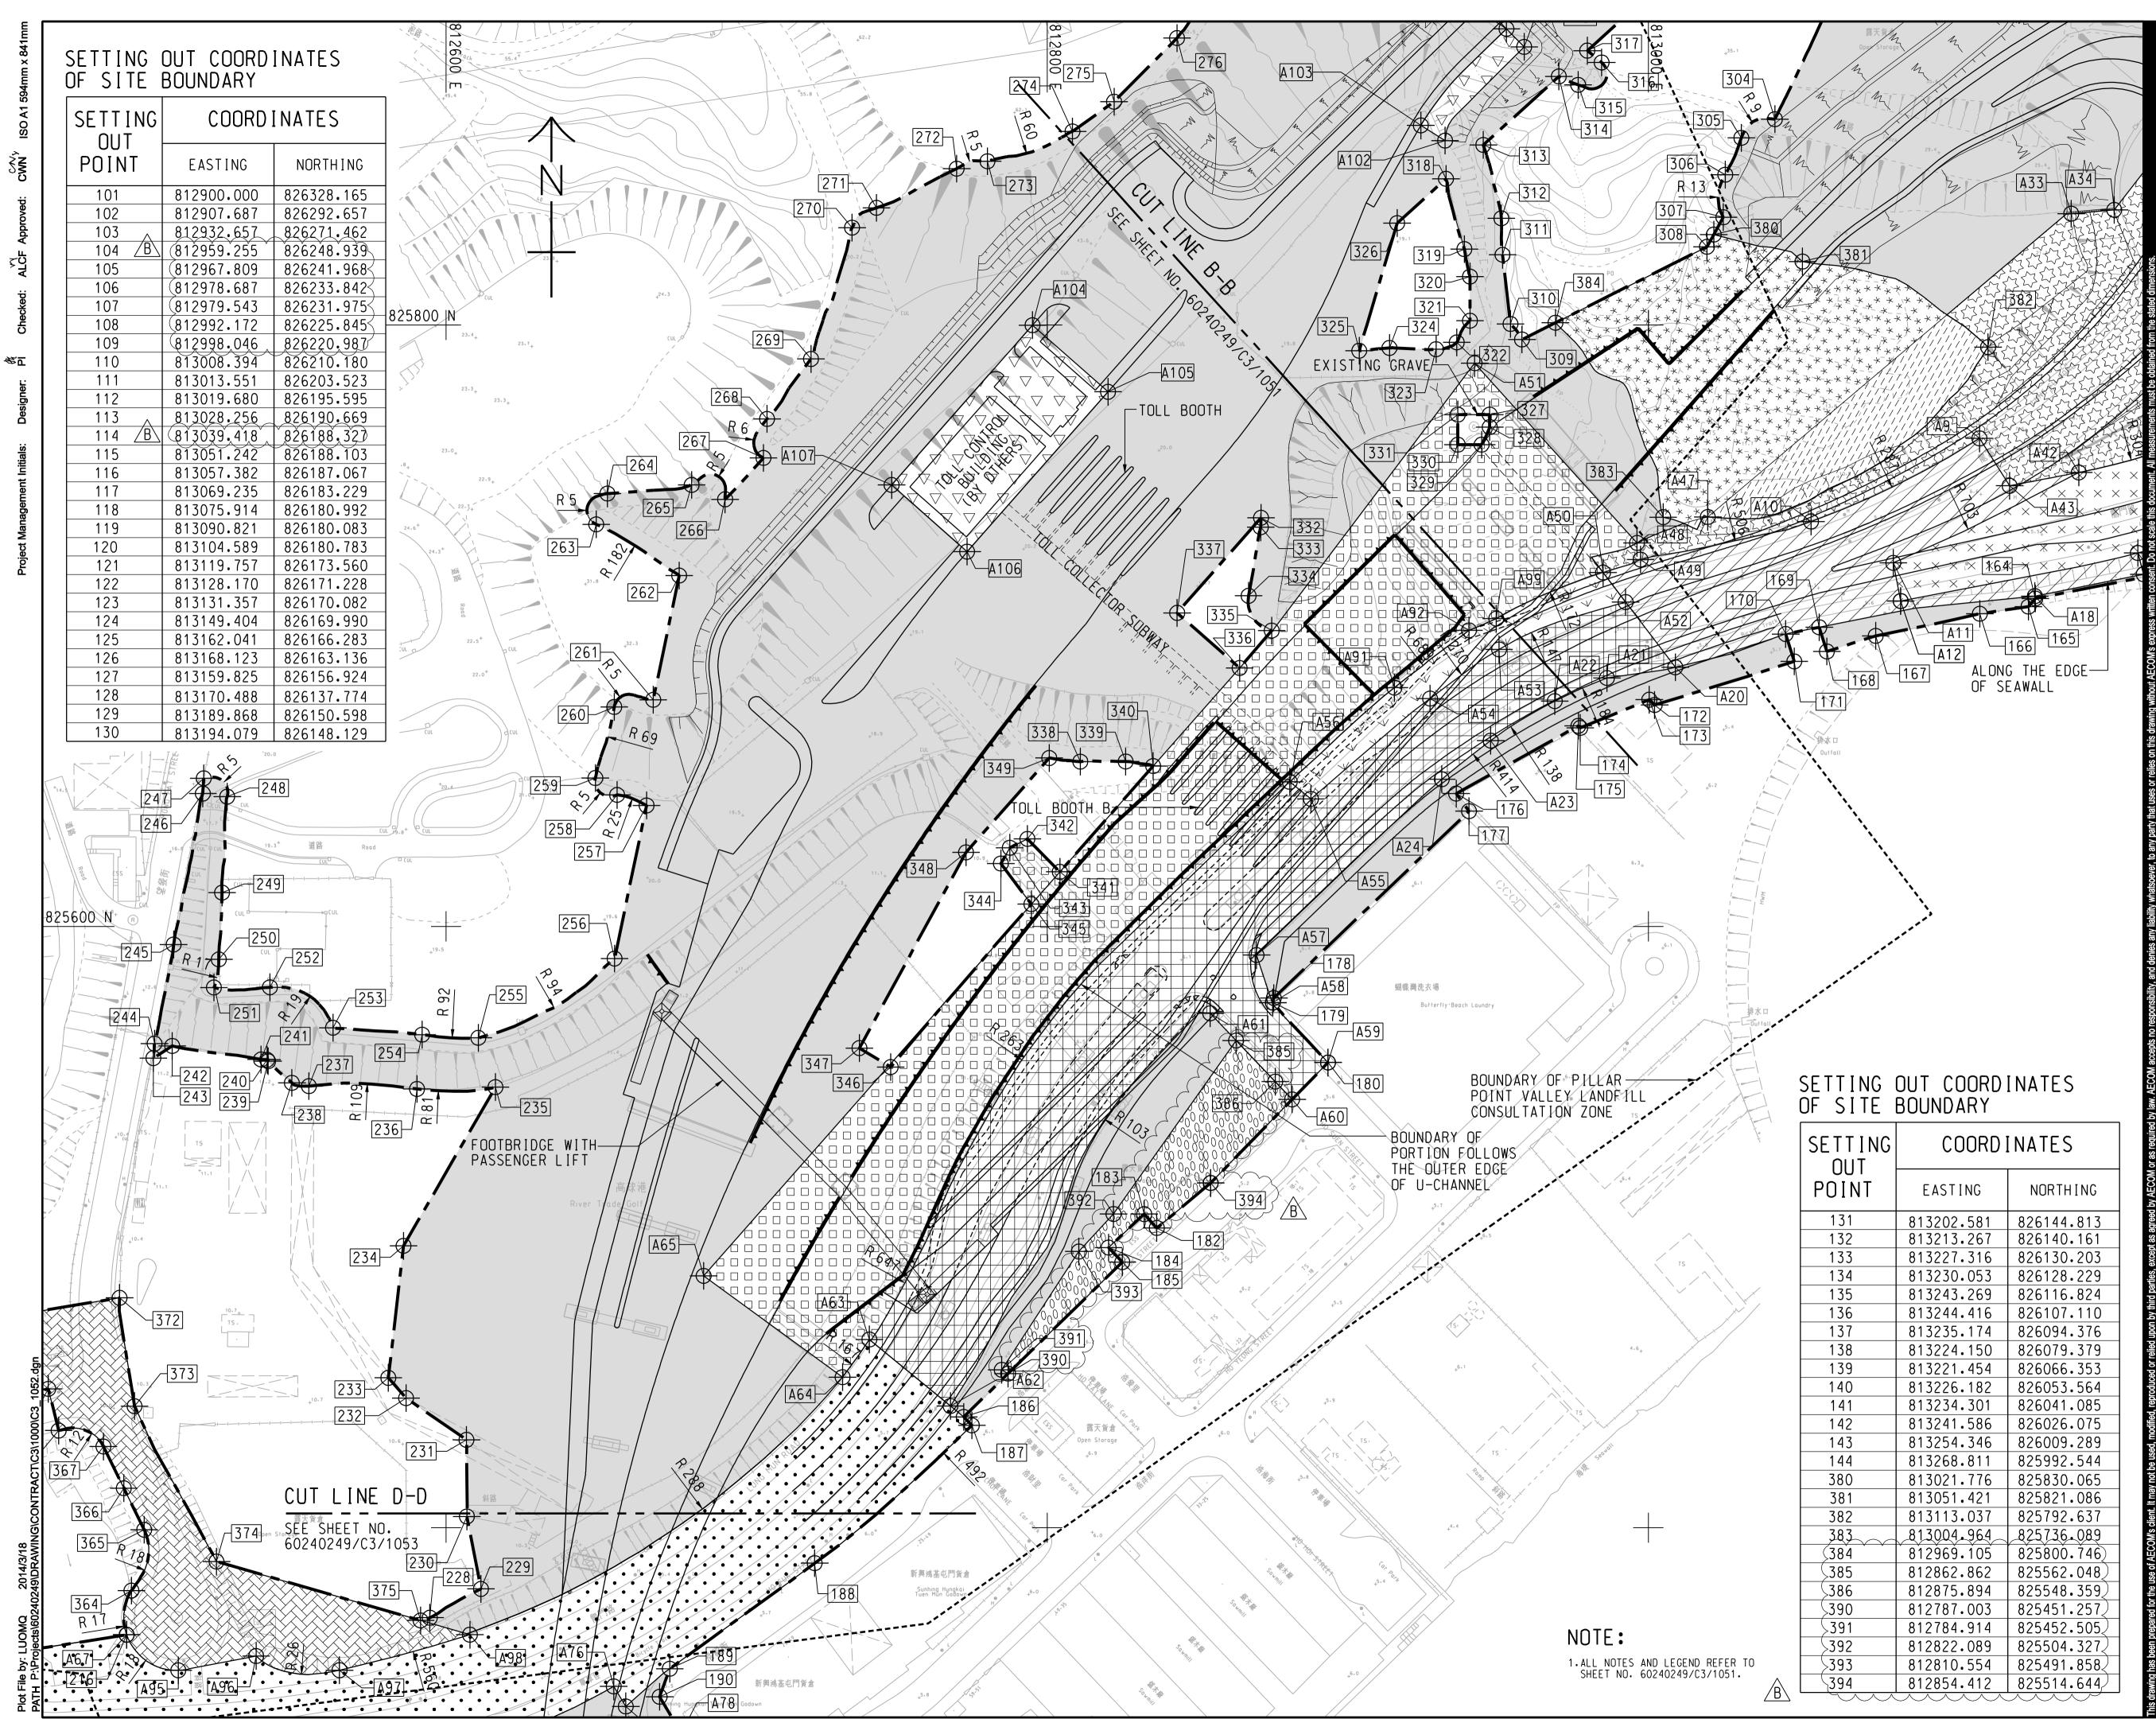

I NG T	COORDINATES			
' IT	EASTING	NORTHING		
	813202.581	826144.813		
	813213.267	826140.161		
	813227.316	826130.203		
	813230.053	826128.229		
	813243.269	826116.824		
	813244.416	826107.110		
	813235.174	826094.376		
	813224.150	826079.379		
	813221.454	826066.353		
	813226.182	826053.564		
	813234.301	826041.085		
	813241.586	826026.075		
	813254.346	826009.289		
	813268.811	825992.544		
	813021.776	825830.065		
	813051.421	825821.086		
	813113.037	825792.637		
$\sim\sim$	813004.964	825736-089		
	812969.105	825800.746)		
	812862.862	825562.048		
	812875.894	825548.359		
	812787.003	825451.257		
	812784.914	825452.505		
	812822.089	825504.327		
	812810.554	825491.858		
	812854.412	825514.644		



# PROJECT <sub>項目</sub>

TUEN MUN -CHEK LAP KOK LINK

CONTRACT TITLE TUEN MUN - CHEK LAP KOK LINK -NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

# CLIENT <sup>業主</sup>



■▲■ 路政署 HIGHWAYS DEPARTMENT 港 珠 澳 大 橋 香 港 工 程 管 理 處 Hong Kong - Zhuhai - Macao Bridge Hong Kong Project Management Office

# **CONSULTANT** 工程顧問公司

AECOM Asia Company Ltd. www.aecom.com

# SUB-CONSULTANTS 分判工程順問公司

## ISSUE/REVISION 修訂

<b>I/R</b> 修訂	DATE 日期	DESCRIPTION 內容摘要	CHK. 複核
-	JAN. 14	TENDER DRAWING	CWŃ
Α	FEB. 14	TENDER ADDENDUM NO. 1	CWN
в	MAR. 14	<b>TENDER ADDENDUM NO. 2</b>	CWN
			CN4

## STATUS 階段

SCALE 比例


A1 1 : 1000

## DIMENSION UNIT <sup>尺寸單位</sup>

METRES

**KEY PLAN** 索引歐引圖

1 : 50000



# PROJECT NO. <sub>項目編號</sub>

CONTRACT NO. <sup>合約編號</sup>

60240249

SHEET TITLE 圖紙名稱


PORTIONS OF SITE AND SITE BOUNDARY SETTING OUT PLAN

# SHEET NUMBER 圖紙編號

60240249/C3/1052B

- HY/2013/12

SHEET 2 OF 3

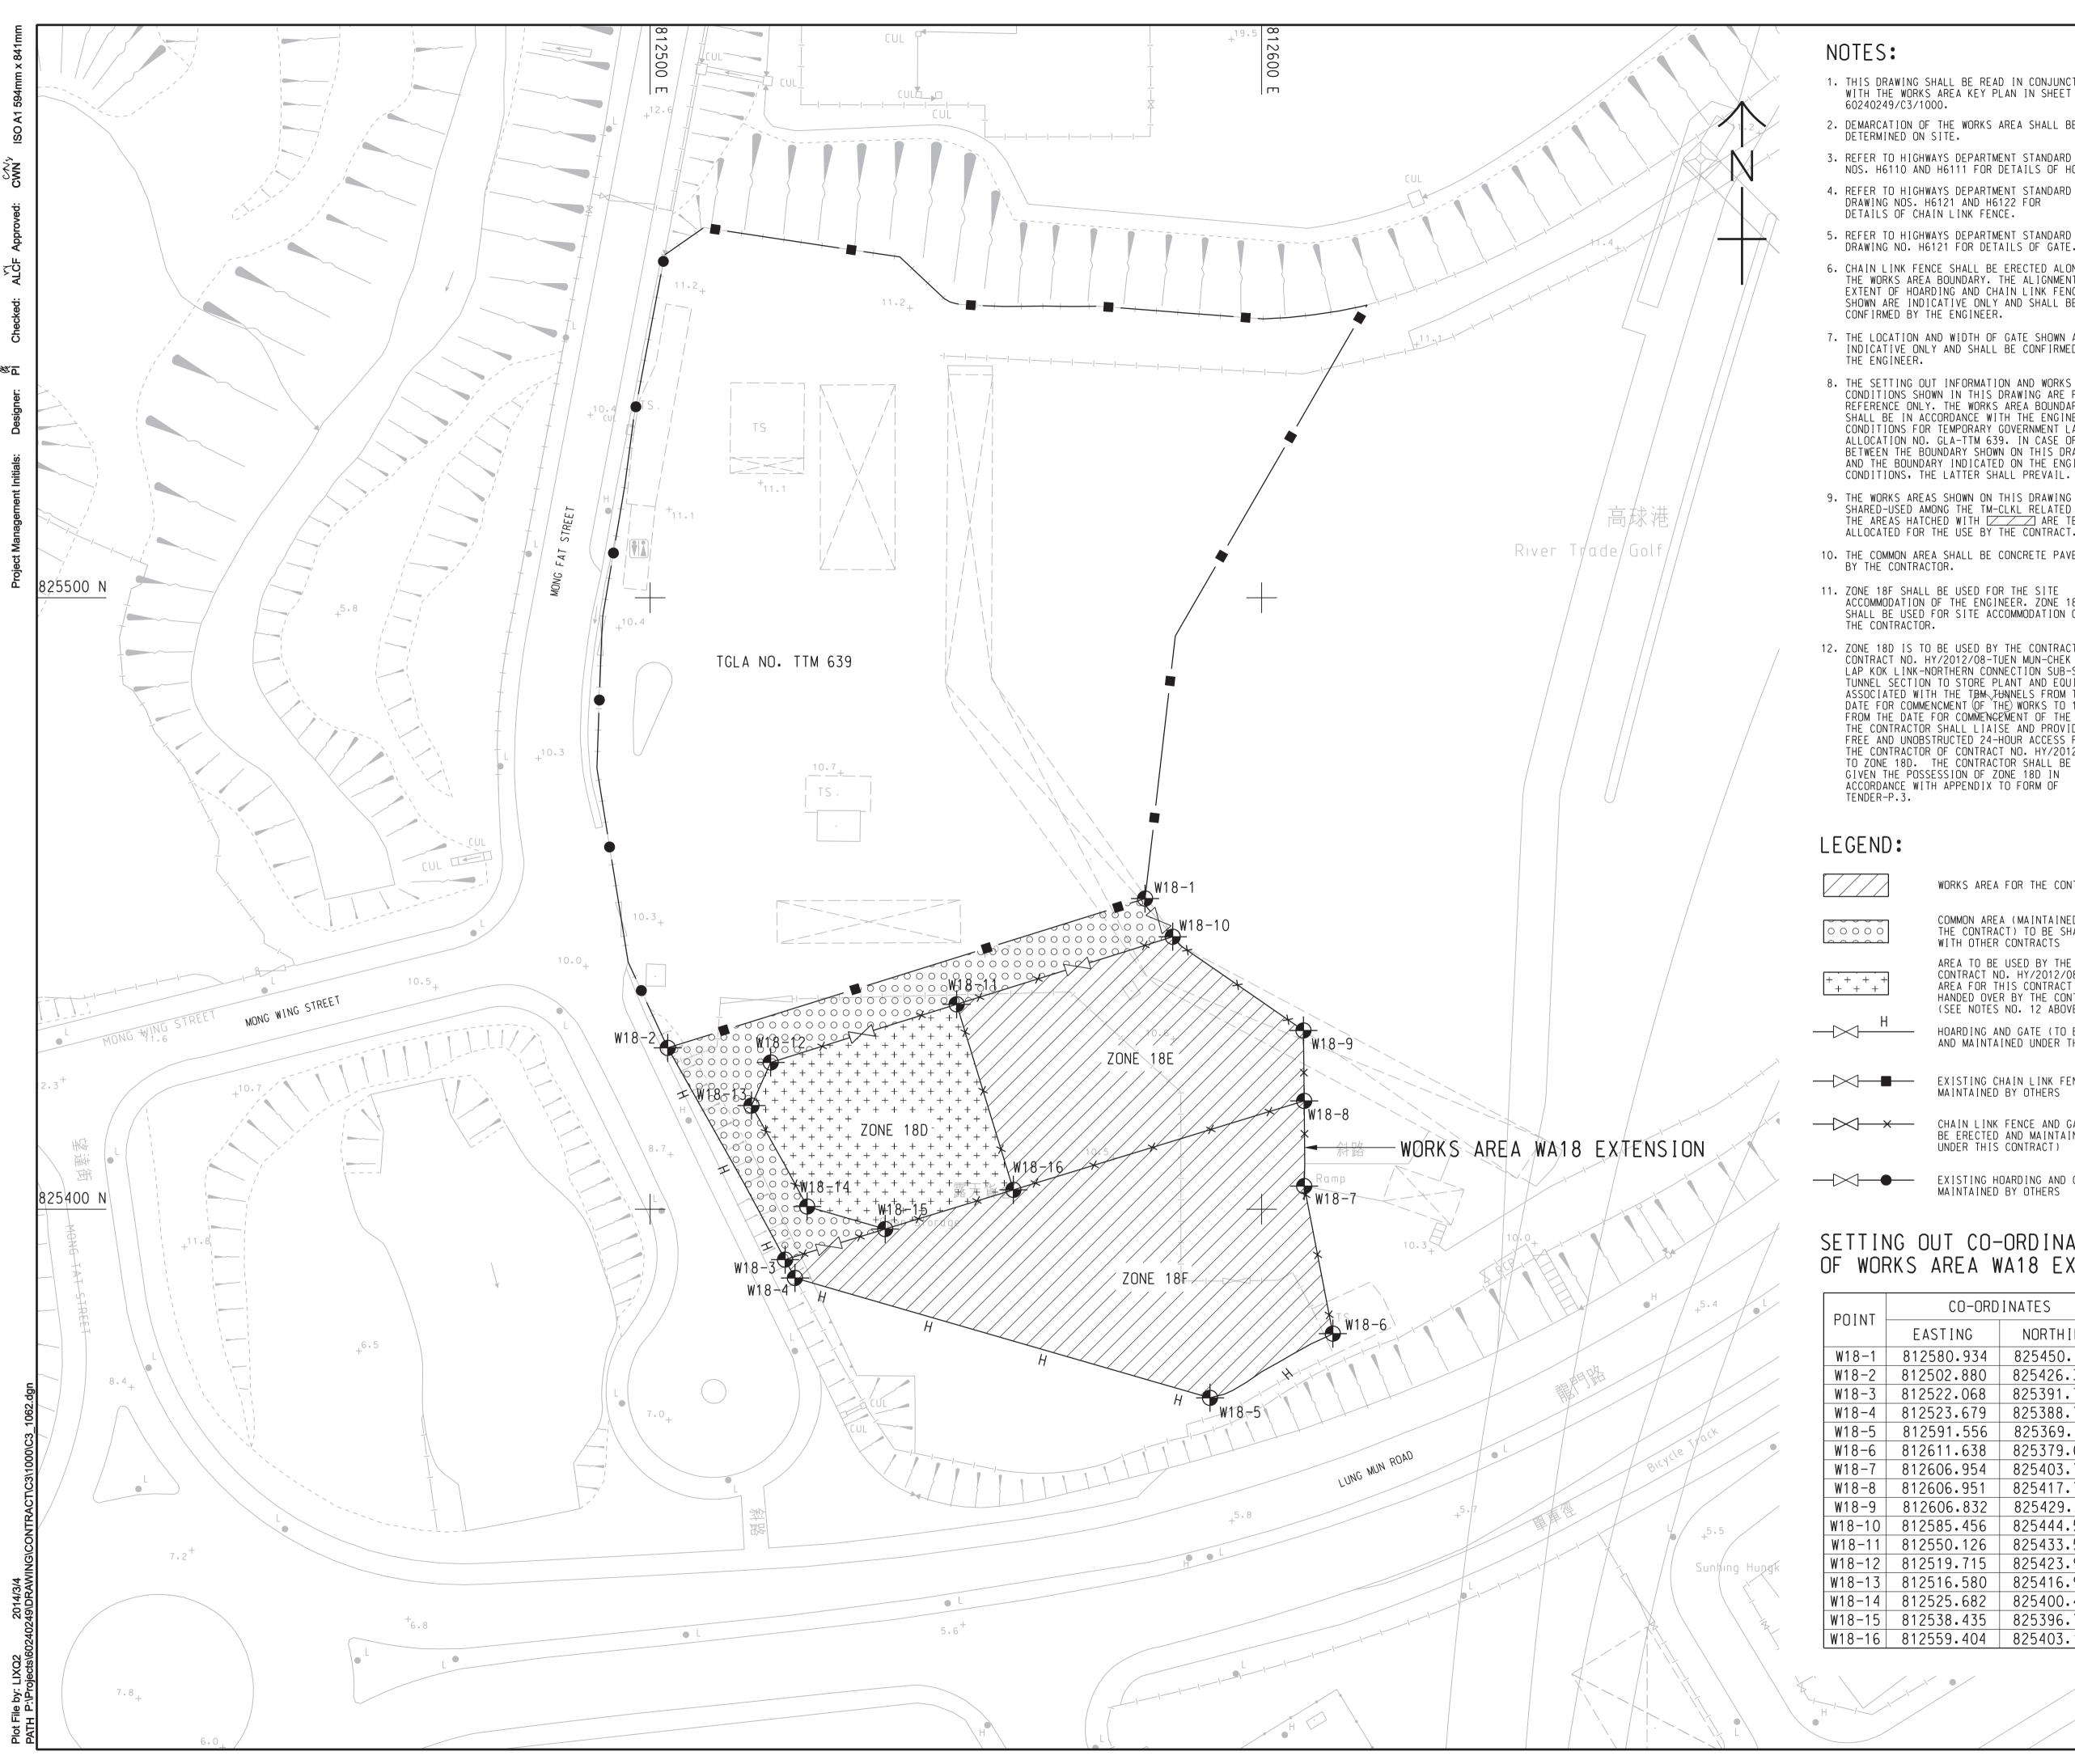

50 €∎

1. THIS DRAWING SHALL BE READ IN CONJUNCTION WITH THE WORKS AREA KEY PLAN IN SHEET NO. 60240249/C3/1000.

2. DEMARCATION OF THE WORKS AREA SHALL BE DETERMINED ON SITE.

3. REFER TO HIGHWAYS DEPARTMENT STANDARD DRAWING NOS. H6110 AND H6111 FOR DETAILS OF HOARDING. 4. REFER TO HIGHWAYS DEPARTMENT STANDARD

DRAWING NOS. H6121 AND H6122 FOR DETAILS OF CHAIN LINK FENCE.

DRAWING NO. H6121 FOR DETAILS OF GATE.

6. CHAIN LINK FENCE SHALL BE ERECTED ALONG THE WORKS AREA BOUNDARY. THE ALIGNMENT AND EXTENT OF HOARDING AND CHAIN LINK FENCE SHOWN ARE INDICATIVE ONLY AND SHALL BE CONFIRMED BY THE ENGINEER.

7. THE LOCATION AND WIDTH OF GATE SHOWN ARE INDICATIVE ONLY AND SHALL BE CONFIRMED BY THE ENGINEER.

8. THE SETTING OUT INFORMATION AND WORKS AREA CONDITIONS SHOWN IN THIS DRAWING ARE FOR REFERENCE ONLY. THE WORKS AREA BOUNDARY SHALL BE IN ACCORDANCE WITH THE ENGINEERING CONDITIONS FOR TEMPORARY GOVERNMENT LAND ALLOCATION NO. GLA-TTM 639. IN CASE OF DISCREPANCY BETWEEN THE BOUNDARY SHOWN ON THIS DRAWING AND THE BOUNDARY INDICATED ON THE ENGINEERING CONDITIONS, THE LATTER SHALL PREVAIL.

9. THE WORKS AREAS SHOWN ON THIS DRAWING ARE TO BE SHARED-USED AMONG THE TM-CLKL RELATED CONTRACTS. THE AREAS HATCHED WITH ZARE TENTATIVELY ALLOCATED FOR THE USE BY THE CONTRACT.

10. THE COMMON AREA SHALL BE CONCRETE PAVED BY THE CONTRACTOR.

11. ZONE 18F SHALL BE USED FOR THE SITE ACCOMMODATION OF THE ENGINEER. ZONE 18E SHALL BE USED FOR SITE ACCOMMODATION OF THE CONTRACTOR.

12. ZONE 18D IS TO BE USED BY THE CONTRACTOR OF CONTRACT NO. HY/2012/08-TUEN MUN-CHEK LAP KOK LINK-NORTHERN CONNECTION SUB-SEA TUNNEL SECTION TO STORE PLANT AND EQUIPMENT B ASSOCIATED WITH THE TEM TUNNELS FROM THE DATE FOR COMMENCMENT (OF THE) WORKS TO 126 DAYS FROM THE DATE FOR COMMENCEMENT OF THE WORKS. THE CONTRACTOR SHALL LIAISE AND PROVIDE FREE AND UNOBSTRUCTED 24-HOUR ACCESS FOR THE CONTRACTOR OF CONTRACT NO. HY/2012/08 TO ZONE 18D. THE CONTRACTOR SHALL BE GIVEN THE POSSESSION OF ZONE 18D IN ACCORDANCE WITH APPENDIX TO FORM OF

WORKS AREA FOR THE CONTRACT

COMMON AREA (MAINTAINED UNDER THE CONTRACT) TO BE SHARED-USED WITH OTHER CONTRACTS AREA TO BE USED BY THE CONTRACTOR OF CONTRACT NO. HY/2012/08 AND WORKS AREA FOR THIS CONTRACT TO BE EARLY HANDED OVER BY THE CONTRACTOR (SEE NOTES NO. 12 ABOVE)

HOARDING AND GATE (TO BE ERECTED AND MAINTAINED UNDER THIS CONTRACT)

EXISTING CHAIN LINK FENCE MAINTAINED BY OTHERS 

CHAIN LINK FENCE AND GATE (TO BE ERECTED AND MAINTAINED UNDER THIS CONTRACT)

EXISTING HOARDING AND GATE MAINTAINED BY OTHERS

# SETTING OUT CO-ORDINATES OF WORKS AREA WA18 EXTENSION

CO-ORDINATES	
EASTING	NORTHING
812580.934	825450.791
812502.880	825426.380
812522.068	825391.750
812523.679	825388.756
812591.556	825369.151
812611.638	825379.647
812606.954	825403.769
812606.951	825417.705
812606.832	825429.231
812585.456	825444.557
812550.126	825433.508
812519.715	825423.997
812516.580	825416.947
812525.682	825400.438
812538.435	825396.754
812559.404	825403.166

AECOM

PROJECT <sup>項目</sup>

TUEN MUN -CHEK LAP KOK LINK

CONTRACT TITLE TUEN MUN - CHEK LAP KOK LINK -NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

# CLIENT 業主



路政署 HIGHWAYS DEPARTMENT 港珠澳大橋香港工程管理處 Hong Kong - Zhuhai - Macao Bridge Hong Kong Project Management Office

## **CONSULTANT** 工程顧問公司

AECOM Asia Company Ltd. www.aecom.com

## SUB-CONSULTANTS 分判工程顧問公司

## **ISSUE/REVISION**

			CNU
в	MAR. 14	<b>TENDER ADDENDUM NO. 2</b>	CWN
Α	FEB. 14	TENDER ADDENDUM NO. 1	CWŃ
-	JAN. 14	TENDER DRAWING	CWŃ
<b>I/R</b> 修訂	DATE 日期	DESCRIPTION 內容摘要	CHK. 複核

## STATUS 階段

SCALE <sup>比例</sup>

## DIMENSION UNIT <sup>尺寸單位</sup>

A1 1 : 500

METRES

KEY PLAN 索引圖

# PROJECT NO. <sub>項目編號</sub>

# CONTRACT NO. <sup>合約編號</sup>

60240249

HY/2013/12

SHEET TITLE 圖紙名稱

WORKS AREA AND HOARDING PLAN

SHEET 2 OF 2

# SHEET NUMBER 圖紙編號


60240249/C3/1062B



# Appendix C

## **Organization of the Contract**



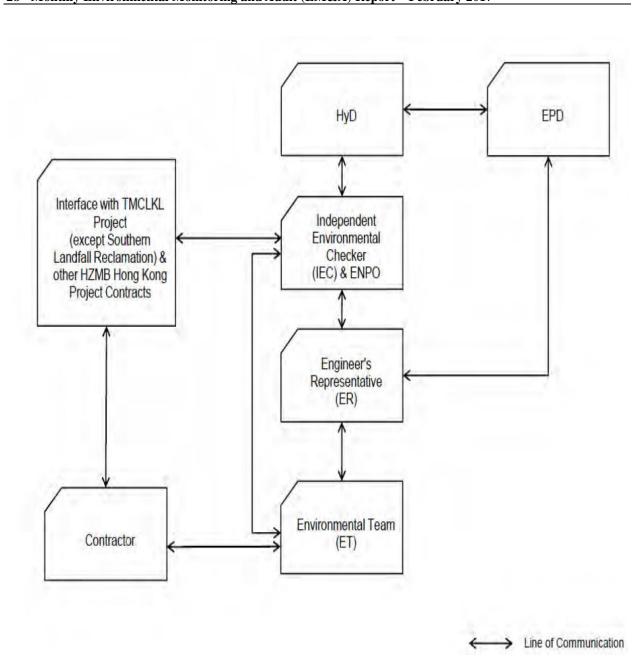

**Project Organization chart** 



Organization	Project Role	Name of Key Staff	Tel No	Fax No.
HyD Employer		Mr. Stephen W.C. Chan	2762 3669	3188 6614
AECOM	Principal Resident Engineer	Mr. S.W. Fok	2218 7209	2218 7399
AECOM	Chief Resident Engineer	Mr. Roger Man	2218 7288	2218 7399
AECOM	Resident Engineer (S&E)	Mr. Kelvin Yeung	22187289	2218 7399
Ramboll Environ	Environmental Project Office (ENPO)	Mr. YH Hui	3465 2850	3465 2899
Ramboll Environ	Independent Environmental Checker (IEC)	Dr. FC Tsang	3465 2851	3465 2899
СКЈV	Deputy Project Manager	Mr. Raymond Suen	2253 8309	2253 8399
СКЈУ	Site Agent	Mr. Wilson Lau	2253 8300	2253 8399
СКЈУ	Safety and Environmental Manager	Mr. Winson Chung	2273 3185	2375 3655
СКЈV	Environmental Officer	Mr. HY Tang	2253 8300	2253 8399
СКЈУ	Environmental Supervisor	Mr. Alex Li	2253 8300	2253 8399
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES Environmental Consultant		Miss Nicola Hon	2959 6059	2959 6079
AUES Environmental Consultant		Mr. Ben Tam	2959 6059	2959 6079
HKL	Registered Landscape Architect	Kenneth Ng	2866 3903	

## Contact Details of Key Personnel for the Contract HY/2013/12

Legend:

HyD (Employer) –Highways Department

AECOM (Engineer) – AECOM Asia Co. Ltd.

CKJV (Main Contractor) – CRBC-Kaden Joint Venture

Ramboll Environ (ENPO and IEC) – Ramboll Environ Hong Kong Limited

AUES (ET) – Action-United Environmental Services & Consulting

HKL(RLA) – Hong Kong Landscape



# Appendix D

## **Three-Months Rolling Programme**

ъ	1
Page	
I age.	1



	Activity Name		2017
2013/12 TMCL	K Northern Connection Toll Plaza and Associated-Works Programme-Rev.4A	Feb Mar	Apr
	tages/ Completion of Sections	▼ Achievement of Stages/	Completion of Sections
KD10170	KD7 - Sec 4 Completion All Works with in Portion D in cl EM&A Implementation	◆ KD7 - Sec 4 Completion	All Works within Portion D incl EM&Al
oll Plaza Decking	a TD1-Section 1		
Stage 1			
	t Submission and Approval	Method Statement Submission an	d Approval
TD121360	Engineer's comments and approval	Engineer's comments and approva	1
Field Works			
Portal Construct	ion		
Portal Beam 1st	(H)		
TD121180	Portal beam 1st(Portal H -Pier 18 to Pier 19)		
Portal Beam 2nd	a(J)		
TD121190	Portal beam 2nd(Portal J -Pier 20 to Pier 21)		
Portal Beam 3rd	(G)		
TD121200	Portal beam 3rd(Portal G -Pier 16 to Pier 17)		
Deck Construction	on		
Precast beam fa	brication	· · · · · · · · · · · · · · · · · · ·	
TD120800	Precast parapet and planter		
Precast beam in	stallation		
TD12100	Precast beam installation between portal H and portal J (4nos)		
TD12110	Precast beam installation between portal G and portal H(4nos)		
TD12120	Precast beam installation between portal H and portal J(3nos)		
TD12130	Precast beam installation between portal J and portal K(4nos)		
In-situ Deck and	Precast Beam		▼ In-situ Deck ar
TD121100	In-situ deck and precast beam between portal D and portal E		
TD121090	In-situ deck and precast beam between portal F and portal G	In-situ deck and precas	t beam between portal F and portal G
TD121105	In-situ deck and precast beam between portal C and portal D	In-situ deck and precas	t beam between portal C and portal D
TD121110	In-situ deck and precast beam between portal B and portal C		In-situ deck and precast beam betw
TD121120	In-situ deck and precast beam between portal G and portal H		In-situ deck and precast beam betw
TD121130	In-situ deck and precast beam between portal H and portal J		In-situ deck and pre-
TD121140	In-situ deck and precast beam between portal J and portal K		In-situ deck and pre
TD121150	M.J installation		M.J installation
Toll Booth Cano	ру		<b>v</b>
Toll both canopy	/ and island		▼
TD121270	Toll booth island		
II Plaza Decking	g TD2-Section 1		
Field Works			
<ul> <li>Remaining Level</li> </ul>	of Effort Critical Remaining Work	CRBC - Kaden JV	Date Rev 03-17
Actual Work	♦ ♦ Milestone Th	ree-Month Rolling Programme	

中國路德 CRBC KADEN Joint Venture				
		May		Jun
nplementatio	on			
Precast Bear	m			
en portal B a	nd portal C			
en portal G a	nd portal H			
st beam betv	veen portal H a	and portal J		
st beam betv	veen portal J a	nd portal K		
ion		Checked	Арр	roved

Page: 2		HY/2013/12 TM-CLKL Northern Cor	nnection Toll Plaza and Associated Works	RB
				CRBC
Activity ID	Activity Name			2017

					CRBC
ity ID	Activity Name		Feb	Mar	2017 Apr
G.I and Piling Work	ts				
DWP-Bored Piles					
TD220530	Working platform for pile cap L4				
TD220540	Bored piles for P12-13				
Deck Construction					
TD220190	Bearing,formwork, reinforcemnt& Concreting-North				Bearing,for
TD220200	Bearing,formwork, reinforcemnt& Concreting-South				
Miscellaneous Wor	ks			neous Works	
TD220695	Cascade D construction		Cascade	D construction	
Toll Plaza Footbrid	ge-Section 1				
Stage 1					
Method Statement	Submissions and Approval		-		• Method Statement S
TFB1090	MSS for concrete slab and planter construction over steel truss				MSS for concrete sl
Off-site Works			▼ Off-site \	Works	
TFB1100	Steel truss fabrication		Steel trus	sfabrication	
Field Works					
Pier Construction				Pier Construction	
TFB1320	Construct pier P6		Co	nstruct pier P6	
TFB1310	Construct pier P4			Construct pier P4	
Steel Truss Install	ation		▼		Steel Truss Installation
TFB1330	Steel truss assembly and installation			Steel truss assembly	y and installation
TFB1340	Steel truss connection				Steel truss connection
Staircase and Lift	Construction				
TFB1350	West staircase construction				W
TFB1370	East staircase construction				
TFB1380	Lift construction B				
TFB1360	Lift construction A				
Concrete Decking	, Planters and Finishing Works				
TFB1390	Concrete decking and planter construction				
Retaining Structure	a RW B-Section 1				
	etaining Structure RW_B				
Stage 1					
Retaining Structur	re RW B				
	lab, Wall, Colume, Top Slab)		Struct	ure(Base Slab, Wall, Colume, Top	Slab)
Bay12-13			Bay12		
RWB10170	Bay12-13 and backfilling		-	2-13 and backfilling	
Backfilling	,		5		
Remaining Level c	of Effort Critical Remaining Work	CRRC	2 - Kaden JV	Dat	
Actual Work	<ul> <li>♦ Milestone</li> </ul>			03-03-17	

Remaining Level of Effort			CRBC - Kaden JV		
Actual Work		♦ Milestone		03-03-17	
	•	▼ Wilestone	Three-Month Rolling Programme		
Remaining Work		Summary			<u>I</u>

▶ 中國路稿 CRBC Kaden <mark></mark> <sup>提</sup>						
BC - KADEN Joint Venture						
		Мау		Jun		
g,formwork, re	inforcemnt& (	Concreting-North				
ent Submissio	ns and Approx	val				
ete slab and pl	anter construc	tion over steel trus	ss			
West staire	ase constructi	on				
	Ea	st staircase constr	ruction			
			🗖 Lift o	onstruction		
			- 1.11100			
vision		Chapter	۸	roued		
vision		Checked	Арр	roved		
			I			

ъ	2
Page	-
I age.	5



		CRE
	Activity Name	2017           Feb         Mar         Apr
RWB10230		Backfilling
RWB10260	•	
oll Collector Su	ubway & Associated Works-Section 1	
Toll Collector B	ridge (Portion I)-Section 1	· · · · · · · · · · · · · · · · · · ·
Stage 1		· · · · · · · · · · · · · · · · · · ·
Temporary Wo	rks Design (TWD) Submission and Approval	$\mathbf{v}$
TCS1240	TWD -Design of lifting system	TWD -Design of lifting system
TCS1580	Engineer's comments and approval	
Field Works		▼ Field Works
TCS1270	Finish the in-situ deck of Bridge TD1(G-H)	◆ Finish the in-situ deck of Bridge TE
Toll Collector S	ubway & Associate Works (Portion I)-Section 1	
Stage 1		
Method Statem	nent Submissions and Approval	Method Statement Submissions and Approval
TCS1630	Engineer's comments and approval	Engineer's comments and approval
Field Works - 1	Toll Collector Subway and Staircase	
TCS1430	Construction of toll collector subway(from SB22-SB16)	Construction of toll collector subway(from SB22-SB16)
TCS1440	Construction of staircase	
Toll Collector S	ubway (Portion X)-Section 5	
Stage 3		
TCS1072	Construct Toll Collector Sub way SB 1	Construct Toll Collector Subway SB 1
TCS1074	Backfill for SB 1	Backfill for SB 1
TCS1130	Construct Toll Collector Sub way SB 9-16	Construct Toll Collector Subway SB 9-16
TCS1090	Hand over Portion D	◆ Hand over Portion D
TCS1140	Backfilling SB2-8	Backfilling SB2-8
TCS1150	Backfilling SB9-16	Backfilling SB9-16
TCS1160	Islands for Toll Booths SB 1-8	
TCS1170	Islands for Toll Booths SB 9-16	
ridge G2		
Stage 2	ks Design (TWD) Submission and Approval	Temporary Works Design (TWD) Submission and Approval
		Engineer's approval
BG23620	Engineer's approval	
Field Works		
Foundation We		
BG23340	Excavation for G2b	
Deck		
BG23050	Deck(G2d1-G2c1)	2c1)
BG23020	Deck(G2c2-G2b)&Construct Portal G2c	
Domaining La	up of Effort Critical Pomoining Work	CDDC V I IV Date Rev
<ul><li>Remaining Lev</li><li>Actual Work</li></ul>	vel of Effort Critical Remaining Work <ul> <li>Milestone</li> </ul>	CRBC - Kaden JV 03-03-17
Remaining Work		Three-Month Rolling Programme

中國路德 CRBC KADEN Joint Venture							
		Мау		Jun			
			Toll Collec	tor Subwa			
	Toll C	Collector Bridge	(Portion I)	Section 1			
	▼ Stage	e 1					
	Temp	oorary Works De	sign(TWD)	) Submissi			
	Engi	neer's comments	and appro	val			
	6		11				
(G-H)							
		<ul> <li>Toll Collector</li> </ul>	r Subway &	t Associate			
		▼ Stage 1					
		Field Works -	- Toll Colle	ctor Subwa			
		Construction	of staircas	e			
			Toll Collec	tor Subwa			
			Stage 3				
		Islands for 7	Foll Booths	SB 1-8			
				Toll Booth			
Deck(G2c2-G2	2b)&Constr	uct Portal G2c					
ion		Checked	Арр	roved			

age: 4		HY/2013/12 TM-CLKL Northern Co	nnection Toll Plaza and A	CRB	
	Activity Name		Feb	Mar	2017
BG23030	Deck(G2b-G2a)		Feb	War	Apr
BG23060	Deck(G2c1-G2b)				
BG23070	Deck(G2b-G2a)		-		
idge G1					
itage 2					
Design Submissio	on and Approval		Design	Submission and Approval	
BG112230	DDA for substructure(draft)				
BG112210	DDA for foundation submission				
BG112220	Engineer's approval				
BG112180	TWD -Form traveller design				
BG112300	Engineer's approval		Engine	eer's approval	
Field Works					
Deck Construction	on from Pier G1d to Pier G2a		· · · · · · · · · · · · · · · · · · ·		
BG112120	Assemble of 1st formtraveller at G1d and testing			Assemble of 1st fo	ormtraveller at G1d and testing
BG112350	Balanced cantilever construction at G1d 1st segment				
BG112360	Assemble of 2nd formtraveller at G1d and testing				
BG112780	TTA application		_		
idge H1-Sectior	n 2				
itage 2					
Design Submissio	on and Approval		Design	Submission and Approval	
BH12860	Engineer's approval		Engine	er's approval	
Field Works					
Decking Constru	uction From Abutment H1f to Pier H1d				
Balanced Canitil	lever Construction at Pier H1e				Balance
BH12028	Balanced cantilever construction at H1e 2nd segment				
BH12030	2nd Pair				
BH12040	3rd Pair				
BH12050	4th Pair		_		
BH12060	5th Pair		5th Pair		
BH12070	6th Pair			6th Pair	
BH12080	7th Pair		-	7th Pair	
BH12090	8th Pair		-	8	8th Pair
	9th Pair		-		9th Pair
BH12110	butment H1f				
BH12110 Insitu Deck at At					
	Construct End Span H1f				
Insitu Deck at Al BH12420	Construct End Span H1 f				
Insitu Deck at Al BH12420					
Insitu Deck at Al BH12420 Balanced Canitil	lever Construction at Pier H1d				
Insitu Deck at Al BH12420 Balanced Canitil	lever Construction at Pier H1d Assemble of 1st formtraveller at H1d	CRB	C - Kaden JV	Da 03-03-17	

中國路稿 CRBC Kaden <u>基</u> 利						
C - KAD	EN Joint V	Venture				
		Мау	Jun			
			Deck(G			
Balanced ca	ntilever constr	uction at G1d 1st				
			Assemble of 21			
nitilever Cor	nstruction at P	ier H1e				
		Balanced Canitiles	ver Construction at			
			rmtraveller at H1d			
		issemble of 1st 10	indiavono at 111u			
ion		Checked	Approved			

Page: 5 HY		HY/2013/12 TM-CLKL Northern Connection Toll P	HY/2013/12 TM-CLKL Northern Connection Toll Plaza and Associated Works			中国路橋 CRBC KADEN Joint Venture			
Activity ID	Activity Name	Feb		Mar	2017 Apr		Мау	Jun	
Culvert 1(TBM)-Sta	age 4					Culvert 1(TBN	I)-Stage 4		
Field Works			Fi	ield Works					
Bay15 to Bay16									
CUL13300	Excavation								
CUL13310	Pipe installation for Bay 15 and 16 and grouting								
FC2			F F	C2					
CUL13470	Construction of chamber FC2								
CUL13480	Backfilling and removal section of sheetpile			ackfilling and removal section of sheetpi	e				
BY-Pass Sewer be	tween FC1 and FC2(1800 Pipe)		BY-Pa	ss Sewer between FC1 and FC2(1800 Pip	e)				
CUL13490	Sheetpile installation for FC2 to FC1								
CUL13500	Excavation and installation of 1800 pipe								
CUL13510	Backfilling		Backf	illing					
Completion of KD	3A and Remaining Works					Completion of	KD3A and Rer	naining Works	
CUL13535	Backfilling					Backfilling			
Culvert 2 & Culver	t 3 and Existing Box Culvert								
Method statemen				▼ Method statem	ent Submission				
CCE20140	Method statement for screeding the existing box culvert			Method statem	ent for screeding the existing box culve	rt			
Culvert 2									
CCE20090	Bay 21				Bay	21			
CCE20120	Bay 20								
Culvert 3									
CCE20212	Drainage diversion		Dra	inage diversion					
CCE20215	MH8								
Existing Sewer Bo									
MH3-MH6									
CCE20220	Base slab to be applied with screeding concrete								
	etainging Structure RW_A						Site For	mation - Retainging	
Stage 3							▼ Stage 3		
Retaining Wall A							Retainir	ng Wall A	
RWA20150	Construct Cascade D			Construct Cascad	le D			C	
RWA20160	Drainage Diversion of Existing Stream to Cascade D				Drainage Diversion of Existing Stream t	o Cascade D			
RWA20180	Backfilling Works				Backfilling Works				
RWA20240	Completion civil provision works for TCSS and E&M						Comple	tion civil provision	
Retaining Structur							-	Structure RW_E	
Stage 2	e Kw_E						Stage 2		
Design Submission	n and Approval							bmission and Appr	
RWE20000	DDA for foundation (draft)			DDA for foundation (dra	(A		Design Du	- mooron and rappi	
KW £20000									
Remaining Level	of Effort Critical Remaining Work	CRBC - Kaden JV		Date	Revision		Checked	Approved	
Actual Work	Milestone	Three-Month Rolling Progr	amme	03-03-17					
Remaining Work	Summary				1	I		1	

Remaining Level of Effort Critical Remaining Work	CRBC - Kaden JV	Date	Revisi
Actual Work $\blacklozenge$ $\blacklozenge$ Milestone	CRBC - Kaden JV	03-03-17	
	Three-Month Rolling Programme		
Remaining Work Summary			

Page: 6			HY/2013/12 TM-CLKL Northern Cor	nection Toll Plaza and A	Associated Wor	ks	中国路 CRBC - KAD	橋 Kaden <sup>基</sup> 利 EN Joint Venture		
tivity ID		Activity Name		Feb	Mar		2017 Apr	Мау	Jun	_
RWE2	20010	Engineer's comments					Engineer's comments			
RWE2	20020	DDA for foundation submission				[	DDA f	or foundation submission		
RWE2	20040	DDA for substructure(draft)						DDA for su	bstructure(draft)	
RWE2	20030	Engineer's approval						Engined	er's approval	
Site Form	nation - Reta	ining Structure for Slope TP_F							Site Formation	- Re
Stage 3									➡ Stage 3	
Retainii	ng Structure fo	or Slope TP_F							<ul> <li>Retaining Struct</li> </ul>	ctur
RWF3	13071	Construct Retaining Wall-Wall construction Bay 20								
RWF3	1308	Backfilling								
RWF3	1480	U-Channel construction, Completion civil provision works for	TCSS and E&M						U-Channel con	istru
Site Form	nation - Slop	e TP_A & Associated Works		· · · · · · · · · · · · · · · · · · ·		Site I	Formation - Slope TP_A & Associated Wo	rks		
Achieve	ment of KD-3	(Stage 3) for Slope A		•		Achi	evement of KD-3(Stage 3) for Slope A			
TPA4180	00	Tunnel Lining Completion		◆ Tunnel Li	ning Completion					
TPA4183	30	Achievement of KD-3(Stage 3) for slope A				<ul> <li>Achie</li> </ul>	evement of KD-3(Stage 3) for slope A			
TPA418	TPA41810     Remaining civil works and draiange works(After tunnel civil works construction)					Rema	ining civil works and draiange works(A	fter tunnel civil works constru	ction)	
Site Form	nation - Slop	e TP_B & Associated Works			<u>.</u>					
Achieve	ment of KD-3	S(Stage 3) for Slope B								
TPB417	10	Remaining civil works and drainage works								
Site Form	nation - Slop	e TP_C & Associated Works					Site Formation - Slope TP_C & Assoc	ated Works		
Achieve	ment of KD-3	I(Stage 3) for Slope C		▼ Achievem	ent of KD-3(Stage 3) f	for Slope C				
TPC5132	20	Achievement of KD-3(Stage 3) for slope C		◆ Achievem	ent of KD-3(Stage 3) f	or slope C				
Achieve	ment of KD-8	(Section 5) for Slope C					Achievement of KD-8 (Section 5) for	Slope C		
TPC5133	30	Remaining works inculde landscape works and establishment	works				Remaining works inculde landscape	works and establishment work	S	
Site Form	nation - Slop	e TP_D & Associated Works		·						
Achieve	ment of KD-7	(Section 4) for Slope D		▼ Achieven	ent of KD-7(Section 4	) for Slope D				
TPD517:	55	Hand over of portion D		◆ Hand ove	of portion D					
Achieve	ment of KD-3	(Stage 3) for Slope D		·						
TPD523	50	Remaining civil works and drainage works			1 1 1					
Site Form	nation - Slop	e TP_E & Associated Works								
Stage 3						▼ Stage 3				
		TP_E at Toll Control Building Area			<ul> <li>Slope Feature - Slop</li> </ul>	e TP_E at Toll Co	ntrol Building Area			
TPE61	1190	U-channel (150m) and Berm for slope E2b								
TPE61	1240	Excavation of Rock for slope E3b - stage 4								
TPE61	1380	U-channel (230m) and Berm for slope E1b and E1c		U-chann	el (230m) and Berm fo	r slope E1b and E	llc			
TPE61	1600	All remaining works include civil provision for TCSS and E&	М	All rem	aining works include c	ivil provision for	TCSS and E&M			
TPE61		Hand Over Portion D			Hand Over Portion I	)				
TPE65	5350	KD-7(Section 4)			◆ KD-7(Section 4)					
					· · · · · ·					
	aining Level of E	ffort Critical Remaining Work	CRBC	C - Kaden JV		Date	Revision	Checked	Approved	
	al Work	Milestone		Rolling Programme		03-03-17				
Kema	aining Work	Summary								

Page: 7



	Activity Name	Feb	Mar	2017 Apr
Slope Feature - S	lope TP_E Remaing Section and 5SE-D/C116	reb		ture - Slope TP_E Remaing Sect
TPE62210	Excavation of Rock for slope E3c - stage 1			
TPE62410	Mapping & Dowelling	□ Mapping &	Dowelling	
TPE62420	U-channel (220m) and Berm for slope E3a		U-channel (220m) and Bern	1 for slope E3a
TPE62600	Construct Cascade C		Construct C	ascade C
TPE62550	Remaining civil works		Remainin	g civil works
TPE62700	Achievement of KD-3(Stage 3) for slope E		◆ Achieven	ent of KD-3(Stage 3) for slope
Achievement of F	KD-8(Section 5) for Slope E		·	
TPE65320	Remaining works inculde landscape works and establishment works			
te Formation - \$	Slope Upgrading Works			
Stage 3 (Other SI				
Slope Feature - 59				
SFW10080	Excavation of Rock (30000m3) for 5SE-D/C170	Excavatio	on of Rock (30000m3) for 5SE-	D/C170
SFW10105	Raking Drain Construction		Raking Drain Construction	
SFW10110	Drainge, U-channel (410m) and Handrailing			
SFW10850	Achievement of KD-3(Stage 3)			
Slope Feature - 55	SE-D/C165			Slope Feature - 5SE-D/C1
SFW10780	Slope Cut and Modification Works (350m3)			
SFW10790	Soil Nail RowC (12nos) Level + 17.60 (Install and grouting)			
SFW10800	Soil Nail RowB (16nos) Level + 15.60 (Install and grouting)			
SFW10810	Soil Nail RowA (19nos) Level + 13.60 (Install and grouting)			
SFW10820	Drainge, U-channel (80m) and Handrailing		Drainge, U-channel (80m) and	Handrailing
SFW10830	Hydroseeding and Erosion Control Mat		Hydroseeding and Erosior	Control Mat
SFW10870	Achievement of KD-3(Stage 3)			Achievement of KD-3(Sta
Slope Feature - 59	SE-D/C150	▼ Slope Feature	- 5SE-D/C150	
SFW10890	Achievement of KD-3(Stage 3)	• Achievement	of KD-3(Stage 3)	
Slope Feature - 59	SE-D/C152		▼ Slope Feature - 5SE-D/C152	
SFW10220	Complete slope 5SE-D/C150			
SFW10240	Drainge, U-channel (90m) and Handrailing		Drainge, U-channel (90m) and	Handrailing
SFW10250	Hydroseeding and Erosion Control Mat		Hydroseeding and Erosion C	ontrol Mat
SFW10910	Achievement of KD-3(Stage 3)		◆ Achievement of KD-3(Stage	3)
Slope Feature - 59	SE-D/C121	▼ Slope Feature	- 5SE-D/C121	
SFW10930	Achievement of KD-3(Stage 3)	◆ Achievement	of KD-3(Stage 3)	
Slope Feature - 55	SE-D/C122	▼ Slope Feature	- 5SE-D/C122	
SFW10950	Achievement of KD-3(Stage 3)	◆ Achievement	of KD-3(Stage 3)	
Slope Feature - 5	SE-D/C14	▼ Slope Feature	- 5SE-D/C14	
SFW10340	Complete TP_F Backfilling(Bay1-2)	◆ Complete [TP]	F Backfilling(Bay1-2)	
Remaining Level	el of Effort Critical Remaining Work	<b>CRBC - Kaden JV</b>	Date	R
Actual Work	♦ ♦ Milestone	Three-Month Rolling Programme	03-03-17	

中國路	稿 C Ka	den 🖁			
KAD	EN Joint V	enture	_		
and for p	(C11)	May			Jun
and 5SE-D	vC116				
			Site	Formation	ı - Slope U
			Stage	e 3 (Other	Slope Fea
			Slop	e Feature	- 5SE-D/C
Durin er I	1 -1 1 (41)	0) 4 11	1		
Drainge, U	J-channel (410				
			Achi	evement o	of KD-3(St
<u>`</u>					
)					
ion		Checked	ł	Арр	roved

Page:	8
I age.	U.



0	Activity Name		2017
AK10410	Possession of Portion X	Feb         Mar           ◆ Possession of Portion X	Apr
Slope Feature - 5S		▼ Slope Feature - 55	SE-D/C149
SFW10380	Complete slope 5SE-D/C152	◆ Complete slope 5	
SFW10990	Achievement of KD-3(Stage 3)	◆ Achievement of k	(D-3(Stage 3)
Slope Feature - 5S		Slope Feature - 55	SE-D/C115
SFW10450	Drainge, U-channel (150m) and Handrailing		
SFW10420	Complete slope 5SE-D/C149		
SFW11010	Achievement of KD-3(Stage 3)	◆ Achievement of k	KD-3(Stage 3)
Slope Feature - 5S			▼ Slope Fea
SFW10550	Slope Modification	Slope Modification	
SFW10560	Rock Mapping and Stabilization		Rock Mapping a
SFW11070	Achievement of KD-3(Stage 3)		◆ Achievem
SFW10570	Hydroseeding and Erosion Control Mat		Hydroseed
Slope Feature - 5S			▼ Slope Fear
SFW10580	Complete slope 5SE-D/C21		◆ Complete
SFW11090	Achievement of KD-3(Stage 3)		◆ Achieven
Slope Feature - 5S			
SFW10630	Slope Modification	Slop	pe Modification
SFW10640	Rock Mapping and Stabilization		
Slope Feature - 5S			
SFW10750	Slope Modification	Slope Modification	
SFW10760	Drainge, U-channel (180m) and Handrailing		
SFW10770	Hydroseeding and Erosion Control Mat		
SFW11170	Achievement of KD-3(Stage 3)		
Vehicular Underpa			
Stage 3			
Lining Works and	Road Works	ind Road Works	
	nd Lining Works	and Lining Works	
Type B			
Lining B1			
UDP4080	Completed the lining works		
Type C			
UDP4250	Formwork for east bulkhead wall	ast bulkhead wall	
UDP4260	Concrete for east bulkhead wall	st bulkhead wall	
	e Work,Utilities Works in Tunnel		
	ge Work,Utilities Works in Tunnel		
UDP34000	DN300	DN300	
Remaining Level	of Effort Critical Remaining Work	CRBC - Kaden JV	Date Revisio
	♦ Milestone	I	()-()-1(

中國路稿 CRBC Kaden <sup>基</sup> 利					
C - KAD	EN Joint V	Venture			
		May		Jun	
	1001				
iture - 5SE-I	9/C21				
and Stabiliz	ation				
nent of KD-	(Stage 3)				
ding and Er	osion Control I	Mat			
ture - 5SE-I	D/C171				
e slope 5SE-l	D/C21				
nent of KD-3					
nent of RD					
	V S	lope Feature - 5SI	E-D/C16		
	F	Rock Mapping and	l Stabiliza	ation	
	• Slope Feat	ure - 5SE-D/C17			
🔲 Draing	e, U-channel (	180m) and Hand	railing		
	Hvdroseed	ling and Erosion C	Control M	at	
		ent of KD-3(Stage			
	Vehicul	ar Underpass TN-	01		
	▼ Stage 3				
	D	Drainage W- 1	T T+;1:+ : :	Worles :- T	
		nd Drainage Work			
	Road ar	nd Drainage Work	Utilities,	Works in T	
ion		Checked	Арр	roved	

Page:	9
	1

## HY/2013/12 TM-CLKL Northern Connection Toll Plaza and Associated Works

CRB

	Activity Name		2017
UDP34010	DN100	Feb Mar DN100	Apr
	PCCW		□ PCCW
UDP34020			Hutchis
UDP34030	Hutchison Global Communication Cable		Hutenis
UDP34040	Hong Kong Boaroband Network		
	e Work ,Utilities Works at for Lung Fu Road Roundabout		
Section 3			
	on ,road and drainage works (TTA stage 0-1)	Utilites installation, road and drainage works (1	TA stage 0-1)
LFR10110	New World Telecom	New World Telecom	
LFR10120	Town Gas	Town Gas	
LFR10130	Smartone Cable	Smartone Cable	
LFR10140	HKC Cable	HKC Cable	
LFR10150	Pubic Lighting	Pubic Lighting	
LFR10160	CLP + CRD	CLP + CRD	
LFR10170	Trax Comm	Trax Comm	
LFR10180	Completion of this stage civil provision for E&M, TCSS	Completion of this stage civil provision for E&M, T	CSS
LFR10060	DN100,300,700	DN100,300,700	
LFR10070	PCCW	PCCW	
LFR10080	Hutchison Global Communication Cable	Hutchison Global Communication Cable	
LFR10090	Hong Kong Boaroband Network	Hong Kong Boaroband Network	
LFR10100	Wharf T&T Duct and Joint Box	Wharf T&T Duct and Joint Box	
LFR10190	Road Pavement	Road Pavement	
LFR10210	TTA for stage 1	◆ TTA for stage 1	
Utilites installatio	n ,road and drainage works (TTA stage 1)	· · · · · · · · · · · · · · · · · · ·	
LFR10270	Filling Works		Filling Works
LFR10300	PCCW		PCCW
LFR10310	Hutchison Global Communication Cable		
LFR10320	Hong Kong Boaroband Network		
LFR10320	Wharf T&T Duct and Joint Box		
LFR10350	New World Telecom		
LFR10340	Town Gas		
LFR10280	Drainage Work		
	je Work ,Utilities Works at Lung Mun Road		
Lung Mun Road			
Ho Suen Street N			
LMRWA1020	DN700 CHH 0 - 69	DN700 CHH 0 - 69	
LMRWA1030	DN200 CHJ 0 - 120	DN200 CHJ 0 - 120	
LMRWA1040	PCCW	PCCW	
			Date
Remaining Leve	l of Effort Critical Remaining Work	CRBC - Kaden JV	

中國路	稿 C Ka	dan <sup>k</sup>		
CRB	C Na	uen 利		
C - KAD	EN Joint V	Venture		
		Мау		Jun
1.1.0				
lobal Comm	unication Cab	le		
		ong Boaroband N	etwork	
				• 10
				- Sec
				▼ Uti
Hutchison (	Slobal Commu	nication Cable		
			1	
	Hong Kon	g Boaroband Netw	VOLK	
		harf T&T Duct an	d Joint B	ox
		New Wo	rld Teleco	om
		Town Ga		
		Town Ga	as	
				Dr
	Ho Sue	n Street North		
ion		Checked	Аррі	roved

Page: 10

## HY/2013/12 TM-CLKL Northern Connection Toll Plaza and Associated Works

CRB

					CRBC -
Activity ID	Activity Name		Feb	Mar	2017 Apr
LMRWA100	00 Drainage Work		rep	Drainage Work	Apr
LMRWA105	50 Hutchison Global Communication Cable			Ηι	tchison Global Communication Cable
LMRWA106	50 Hong Kong Boaroband Network				Hong Kong Boar
LMRWA107	70 Wharf T&T Duct and Joint Box				
Ho Suen Str	eet South				
LMRWA120	DN300 CHE 0 - 116				
LMRWA121	0 DN100 CHG 0 - 112				
LMRWA117	70 Drainage Work				
Utilites instal	lation ,road and drainage works for East Portal				
EPA1000	Rock Cutting				
EPA1020	DN300 CHA 0 - 175&DN100				
Utilites instal	lation ,road and drainage works near portion D				
TOLLA1010	DN300			DN300	)
TOLLA1020	DN100			DN100	)
TOLLA1030	PCCW				PCCW
TOLLA1040	Hutchison Global Communication Cable				
TOLLA1050	Hong Kong Boaroband Network				
Seweage, Irri	gation and Road& Drainage Works				
SAI10060	Seweage, irrigation and road&drainage works -G2-north side	le			
SAI10070	Seweage, irrigation and road&drainage works- G2-south side	le			
SAI10040	Seweage, irrigation and road&drainage works -G1&H1-north	th side			
Achievement	of Key Dates				Achievement of Key Dates
AK10320	Achievement of KD-3(Stage 3) for slope C		◆ Achie	wement of KD-3(Stage 3) for slope C	
AK10365	Achievement of KD-7(Section 4) for slope E			◆ Achievement of KD-7(Section 4	) for slope E
AK10280	Achievement of KD-3(Stage 3) for slope A			•	Achievement of KD-3(Stage 3) for slo
					1


Remaining Level of Effort	CRBC - Kaden JV	Date	Revis
Actual Work $\blacklozenge$ $\blacklozenge$ Milestone	CRBC - Kaden JV	03-03-17	
	Three-Month Rolling Programme		
Remaining Work Summary			


中國路稿 CRBC Kaden 刻					
BC - KAD	EN Joint V	Venture			
		Мау			Jun
Cable					
Boaroband N					
	Wharf	T&T Duct an	d Joi	nt Box	
					Ro
		v	Utili	tes instal	lation ,roa
	Hutchison	Global Com	nuni	cation Ca	ble
			Hong	g Kong Bo	paroband l
1 4					
or slope A					
rision		Checked	ł	Арр	roved
		l		I	




# Appendix E

# **Monitoring Locations / Sensitive Receivers for the Contract**

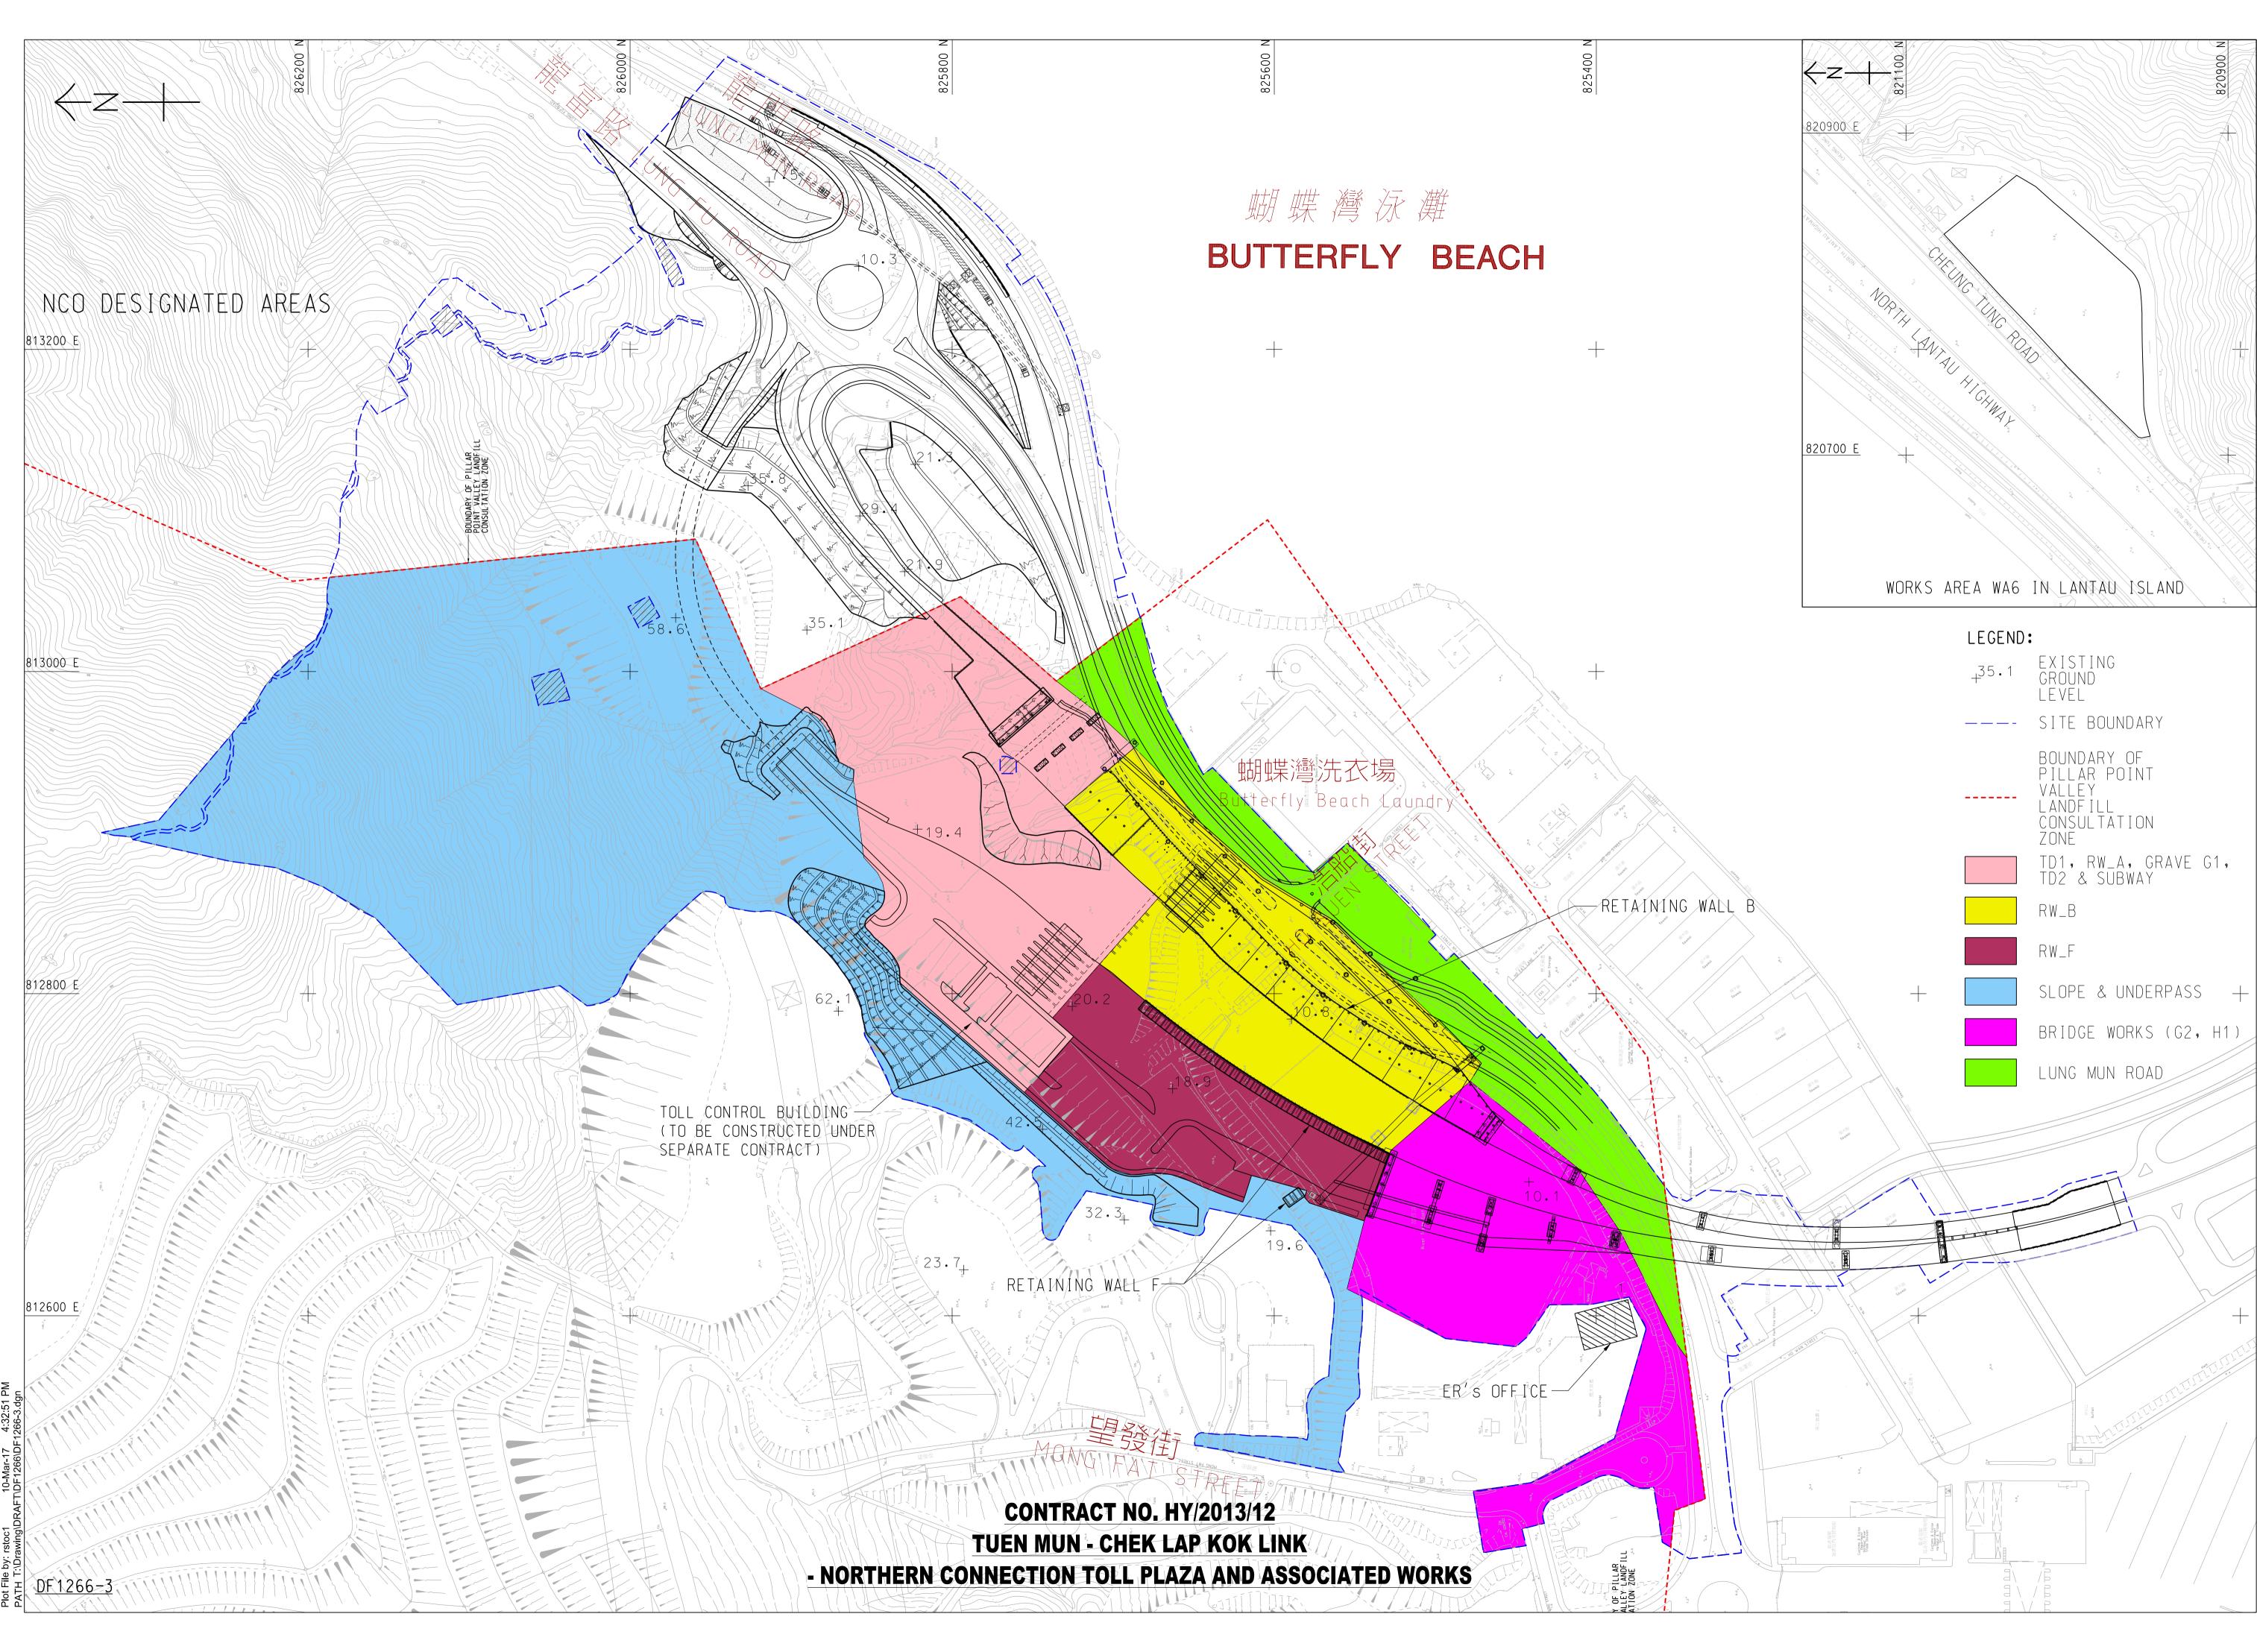

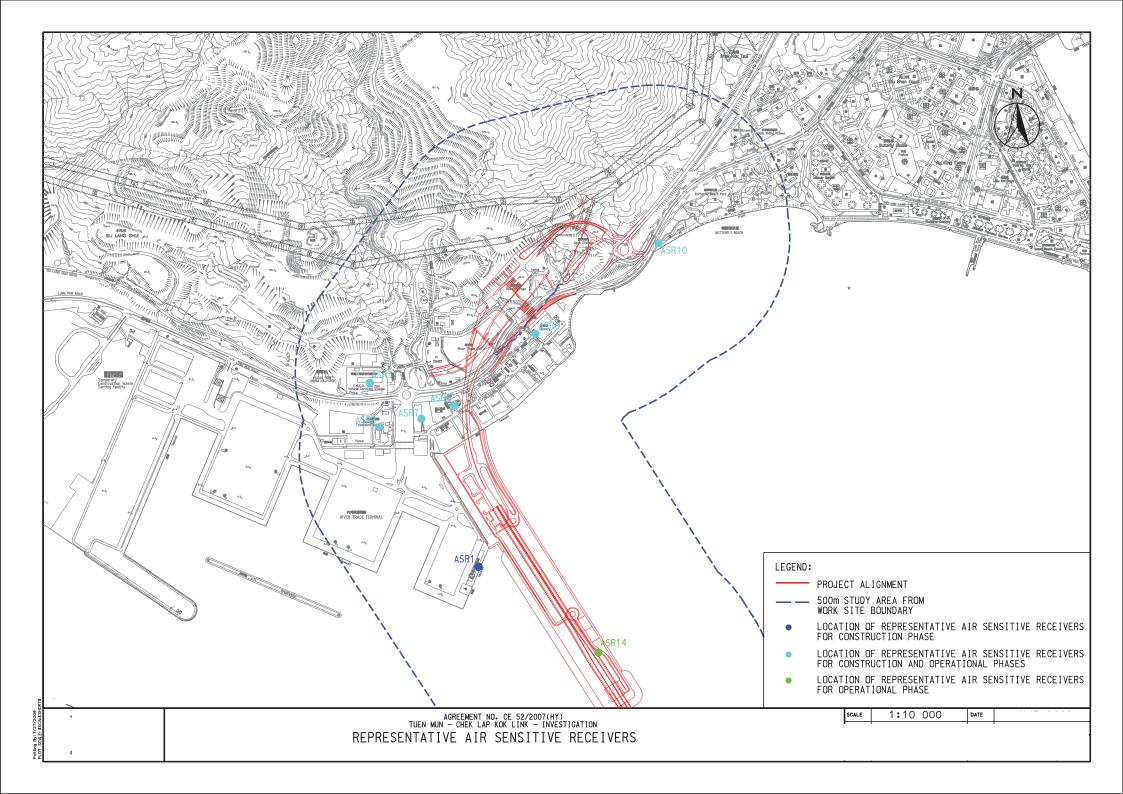




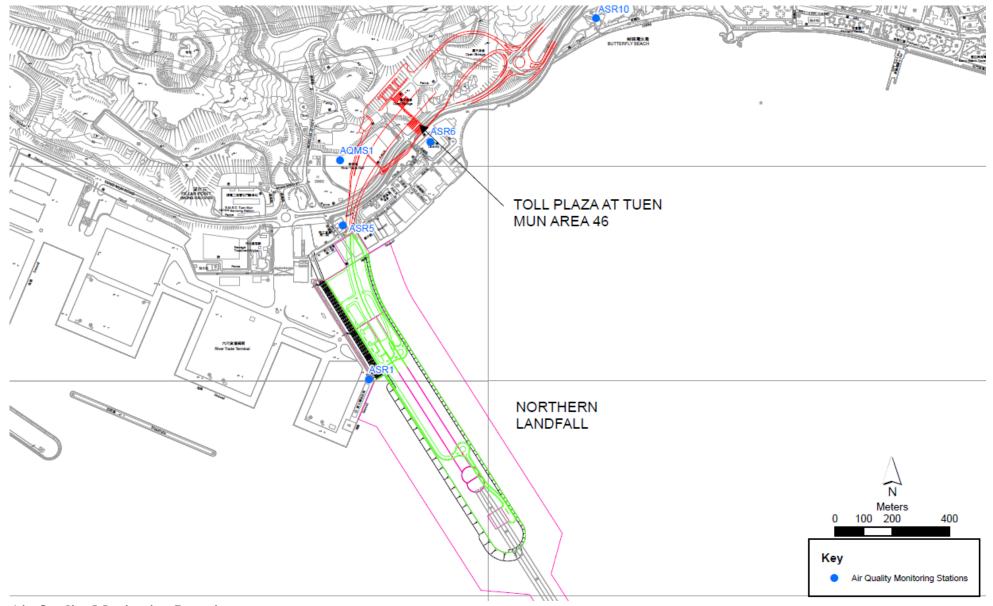


### Air Quality Monitoring Location



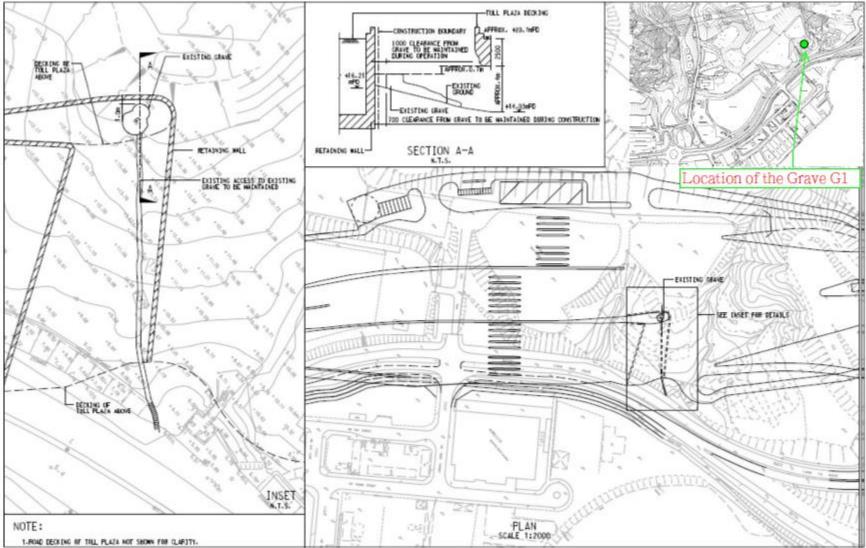

Location of the Grave G1

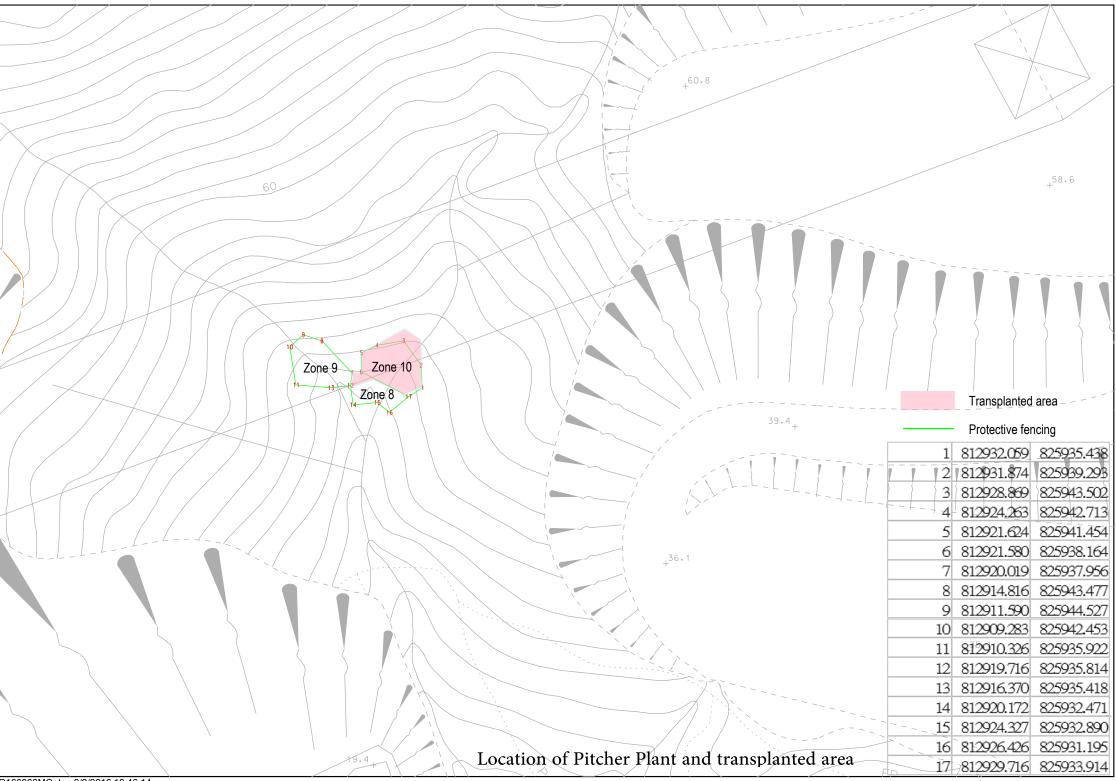

R160908MC.dgn 9/9/2016 10:46:14



Appendix F

# **Event and Action Plan**



#### **Event and Action Plan for Air Quality**

EVENT		ACTION		
	ET <sup>(1)</sup>	IEC <sup>(1)</sup>	SOR <sup>(1)</sup>	Contractor(s)
Action Level		1 (1 1 1		1. D'C
Exceedance recorded	<ol> <li>Identify the source.</li> <li>Repeat measurements to confirm findings. If two consecutive measurements exceed Action Level, the exceedance is then confirmed.</li> <li>Inform the IEC and the SOR</li> <li>Investigate the cause of exceedance and check Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>If the exceedance is confirmed to be Project related after investigation, increase monitoring frequency to daily.</li> <li>Discuss with the IEC and the Contractor on remedial actions required.</li> <li>If exceedance continues, arrange meeting with the IEC and the SOR.</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol> <li>Check monitoring data submitted by the ET.</li> <li>Check the Contractor's working method.</li> <li>If the exceedance is confirmed to be Project related after investigation, discuss with the ET and the Contractor on possible remedial measures.</li> <li>Advise the SOR on the effectiveness of the proposed remedial measures.</li> <li>Supervisor implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing.</li> <li>Notify the Contractor.</li> <li>Ensure remedial measures properly implemented.</li> </ol>	<ol> <li>Rectify any unacceptable practice.</li> <li>Amend working methods if appropriate</li> <li>If the exceedance is confirmed to be Project related, submit proposals for remedial actions to IEC within 3 working days of notification</li> <li>Implement the agreed proposals</li> <li>Amend proposal if appropriate.</li> </ol>
Limit Level				
Exceedance recorded	<ol> <li>Identify the source.</li> <li>Repeat measurement to confirm finding. If two consecutive measurements exceed Limit Level, the exceedance is then confirmed.</li> <li>Inform the IEC, the SOR, the DEP and the Contractor.</li> <li>Investigate the cause of exceedance and check Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>If the exceedance is confirmed to be Project related after investigation, increase monitoring frequency to daily.</li> <li>Carry out analysis of the Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>Arrange meeting with the IEC and the SOR to discuss the remedial actions to be taken.</li> <li>Assess effectiveness of the Contractor's remedial actions and keep the IEC, the DEP and the SOR informed of the results.</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol> <li>Check monitoring data submitted by the ET.</li> <li>Check Contractor's working method.</li> <li>If the exceedance is confirmed to be Project related after investigation, discuss with the ET and the Contractor on possible remedial measures.</li> <li>Advise the SOR on the effectiveness of the proposed remedial measures.</li> <li>Supervisor implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing.</li> <li>Notify the Contractor.</li> <li>If the exceedance is confirmed to be Project related after investigation, in consultation with the IEC, agree with the Contractor on the remedial measures to be implemented.</li> <li>Ensure remedial measures are properly implemented.</li> <li>If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated.</li> </ol>	<ul> <li>action to avoid further exceedance.</li> <li>2 If the exceedance is confirmed to be Project related after investigation, submit proposals for remedial actions to IEC within 3 working days of notification.</li> <li>3 Implement the agreed proposals.</li> <li>4 Amend proposal if appropriate.</li> <li>5 Stop the relevant activity of works as determined by the SOR until the exceedance is abated.</li> </ul>



EVENT	ACTION			
ACTION LEVEL	ET	IEC	ER	Contractor
Design Check	• Check final design conforms to the requirements of EP and prepare report.	<ul> <li>Check report.</li> <li>Recommend remedial design if necessary</li> </ul>	• Undertake remedial design if necessary	
Non- conformity on one occasion	<ul> <li>Identify Source</li> <li>Inform IEC and ER</li> <li>Discuss remedial actions with IEC, ER and Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> </ul>	<ul> <li>Check report</li> <li>Check Contractor's working method</li> <li>Discuss with ET and Contractor on possible remedial measures</li> <li>Advise ER on effectiveness of proposed remedial measures.</li> <li>Check implementation of remedial measures</li> </ul>	<ul> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ul>	<ul> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>
Repeated Non- conformity	<ul> <li>Identify Source</li> <li>Inform IEC and ER</li> <li>Increase monitoring frequency</li> <li>Discuss remedial actions with IEC, ER and Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> <li>If nonconformity stops, cease additional monitoring</li> </ul>	<ul> <li>Check monitoring report</li> <li>Check Contractor's working method</li> <li>Discuss with ET and Contractor on possible remedial measures</li> <li>Advise ER on effectiveness of proposed remedial measures</li> <li>Supervise implementation of remedial measures</li> </ul>	<ul> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ul>	<ul> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>

#### **Event and Action Plan for Landscape and Visual Impact**



			8	<u> </u>
Action Level	ET	IC (E)	ER	Contractor
Non- conformity on one occasion	<ol> <li>Identify Source</li> <li>Inform the IEC and the ER</li> <li>Discuss remedial actions with the IEC, the ER and the Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> </ol>	<ol> <li>Check report</li> <li>Check the Contractor's working method</li> <li>Discuss with the ET and the Contractor on possible remedial measures</li> <li>Advise the ER on effectiveness of proposed remedial measures.</li> <li>Check implementation of remedial measures.</li> </ol>	<ol> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ol>	<ol> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ol>
Repeated Non- conformity	<ol> <li>Identify Source</li> <li>Inform the IC(E) and the ER</li> <li>Increase monitoring frequency</li> <li>Discuss remedial actions with the IC(E), the ER and the Contractor</li> <li>Monitor remedial actions until</li> <li>rectification has been completed</li> <li>If exceedance stops, cease additional monitoring</li> </ol>	<ol> <li>Check monitoring report</li> <li>Check the Contractor's working method</li> <li>Discuss with the ES and the Contractor on possible remedial measures</li> <li>Advise the ER on effectiveness of proposed remedial measures</li> <li>Supervise implementation of remedial measures.</li> </ol>	<ol> <li>Notify the Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ol>	<ol> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ol>

### **Event / Action Plan for Cultural Heritage**

Note:

ET - Environmental Specialist, IEC - Independent Environmental Checker, ER - Engineer's Representative



Action Level	ЕТ	IEC	ER	Contractor
Non- conformity on one occasion	<ul> <li>Identify Source</li> <li>Inform the IEC and the ER</li> <li>Discuss remedial actions with the IEC, the ER and the Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> </ul>	<ul> <li>Check report</li> <li>Check the Contractor's working method</li> <li>Discuss with the ET and the Contractor on possible remedial measures</li> <li>Advise the ER on effectiveness of proposed remedial measures.</li> <li>Check implementation of remedial measures.</li> </ul>	<ul> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> <li>Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the works in the case of a serious nonconformity until situation rectified.</li> </ul>	<ul> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>
Repeated Non conformity	<ul> <li>Identify Source</li> <li>Inform the IC(E) and the ER</li> <li>Increase monitoring frequency</li> <li>Discuss remedial actions with the</li> <li>IC(E), the ER and the Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> <li>If exceedance stops, cease additional monitoring</li> </ul>	<ul> <li>Check monitoring report</li> <li>Check the Contractor's working method</li> <li>Discuss with the ES and the Contractor on possible remedial measures</li> <li>Advise the ER on effectiveness of proposed remedial measures</li> <li>Supervise implementation of remedial measures</li> </ul>	<ul> <li>Notify the Contractor</li> <li>Ensure remedial measures are properly implemented</li> <li>Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the works in the case of a serious nonconformity until situation rectified.</li> </ul>	<ul> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>

#### **Event / Action Plan for General Ecology**

Note:

ET - Environmental Specialist, IC(E) - Independent Checker (Environmental), ER - Engineer's Representative



Parameter	Measurement	Action
Oxygen	< 19%	- Ventilate to restore oxygen to > 19%
	< 18%	<ul> <li>Stop work</li> <li>Evacuate personnel / prohibit entry</li> <li>Increase ventilation to restore to &gt; 19%</li> </ul>
Methane	> 10% LEL (> 0.5% v/v)	<ul><li>Prohibit hot work</li><li>Ventilate to restore methane to &lt; 10% LEL</li></ul>
	> 20% LEL (>1% v/v)	<ul> <li>Stop work</li> <li>Evacuate personnel / prohibit entry</li> <li>Increase ventilation to restore to &lt; 10%</li> </ul>
Carbon Dioxide	> 0.5%	- Ventilate to restore oxygen to $< 0.5\%$
	> 1.5%	<ul> <li>Stop work</li> <li>Evacuate personnel / prohibit entry</li> <li>Increase ventilation to restore to &lt; 0.5%</li> </ul>

## Actions in the Event of Landfill Gas being Detected in Excavation / Confined Area



Appendix G

**Monitoring Schedule** 



	Date	Landfill Gas Monitoring	Landscape and Visual Monitoring
Wed	1-February-17	$\checkmark$	8
Thu	2-February-17	$\checkmark$	
Fri	3-February-17	$\checkmark$	$\checkmark$
Sat	4-February-17	$\checkmark$	
Sun	5-February-17		
Mon	6-February-17	$\checkmark$	
Tue	7-February-17	$\checkmark$	
Wed	8-February-17	$\checkmark$	
Thu	9-February-17	$\checkmark$	
Fri	10-February-17	$\checkmark$	$\checkmark$
Sat	11-February-17	$\checkmark$	
Sun	12-February-17		
Mon	13-February-17	$\checkmark$	
Tue	14-February-17	$\checkmark$	
Wed	15-February-17	$\checkmark$	
Thu	16-February-17	$\checkmark$	
Fri	17-February-17	$\checkmark$	$\checkmark$
Sat	18-February-17	$\checkmark$	
Sun	19-February-17		
Mon	20-February-17	$\checkmark$	
Tue	21-February-17	$\checkmark$	
Wed	22-February-17	$\checkmark$	
Thu	23-February-17	$\checkmark$	
Fri	24-February-17	$\checkmark$	$\checkmark$
Sat	25-February-17	$\checkmark$	
Sun	26-February-17		
Mon	27-February-17	$\checkmark$	
Tue	28-February-17	$\checkmark$	

### **Impact Monitoring Schedule for February 2017**

$\checkmark$	Monitoring Day
	Sunday or Public Holiday



	Date	Landfill Gas Monitoring	Landscape and Visual Monitoring
Wed	1-March-17	$\checkmark$	
Thu	2-March-17	$\checkmark$	
Fri	3-March-17	$\checkmark$	$\checkmark$
Sat	4-March-17	$\checkmark$	
Sun	5-March-17		
Mon	6-March-17	$\checkmark$	
Tue	7-March-17	$\checkmark$	
Wed	8-March-17	$\checkmark$	
Thu	9-March-17	$\checkmark$	
Fri	10-March-17	$\checkmark$	$\checkmark$
Sat	11-March-17	$\checkmark$	
Sun	12-March-17		
Mon	13-March-17	$\checkmark$	
Tue	14-March-17	$\checkmark$	
Wed	15-March-17	$\checkmark$	
Thu	16-March-17	$\checkmark$	
Fri	17-March-17	$\checkmark$	$\checkmark$
Sat	18-March-17	$\checkmark$	
Sun	19-March-17		
Mon	20-March-17	$\checkmark$	
Tue	21-March-17	$\checkmark$	
Wed	22-March-17	$\checkmark$	
Thu	23-March-17	$\checkmark$	
Fri	24-March-17	$\checkmark$	$\checkmark$
Sat	25-March-17	$\checkmark$	
Sun	26-March-17		
Mon	27-March-17	$\checkmark$	
Tue	28-March-17	$\checkmark$	
Wed	29-March-17	$\checkmark$	
Thu	30-March-17	$\checkmark$	
Fri	31-March-17	$\checkmark$	$\checkmark$

# **Impact Monitoring Schedule for March 2017**

$\checkmark$	Monitoring Day
	Sunday or Public Holiday



# Appendix H

# **Calibration Certificates of Monitoring Equipment**

# CERTIFICATION OF CALIBRATION



Date Of Calibration: 13-Jul-2016 Certificate Number: G502306\_2/16764

#### ISSUED BY: GEOTECHNICAL INSTRUMENTS (UK) LTD

Customer: Fugro Geotechnical Services Ltd

Units 6, 8-11 10/F Worldwide Industrial Centre 43-47 Shan Mei Street Fo Tan Sha Tln, N.T. HONG KONG

Description: Gas Analyser

Model: BIOGAS 5000

Serial Number: G502306

#### **UKAS Accredited results:**

Results after adjustment :

Methane (CH₄)			
Certified Gas (%)	Instrument Reading (%)	Uncertainty (%)	
5.1	5.0	0.41	
15.0	14.9	0.64	
50.0	49.4	0.94	

Carbon Dioxide (CO <sub>2</sub> )			
Certified Gas (%)	Instrument Reading (%)	Uncertainty (%)	
5.1	4.9	0.43	
15.1	14.8	0.70	
50.0	49.9	1.1	

	Oxygen (O <sub>2</sub> )	
Certified Gas (%)	Instrument Reading (%)	Uncertainty (%)
21.4	21.5	0.31

The inwards assessment was carried out 11-Jul-2016.

The maximum adjustment is larger than the inwards assessment uncertainty.

Inwards assessment data is available if requested.

All concentrations are molar.

$CH_4$ , $CO_2$ readings recorded at :	31.7 °C ± 1.5 °C
O2 reading recorded at :	22.0 °C ± 1.5 °C
Barometric Pressure :	1011 mbar ± 3 mbar

Method of Test : The analyser is calibrated in a temperature controlled chamber using a series of reference gases, in compliance with procedure LP004.

This certificate is issued in accordance with the laboratory accreditation requirements of the United Kingdom Accreditation Service. It provides traceability of measurement to the SI system of units and/or to units of measurement realised at the National Physical Laboratory or other recognised national metrology institutes. This certificate may not be reproduced other than in full, except with the prior written approval of the issuing laboratory.

Page 1 of 2 | LP015GIUKAS-2.2

🛞 geotechuk.com 🙋 service@geotech.co.uk 📘 +44 (0)1926 338111

Sovereign House, Queensway, Learnington Spa, Warwickshire, CV31 3JR

# **CERTIFICATION OF CALIBRATION**



Date Of Calibration: 13-Jul-2016 Certificate Number: G502306\_2/16764

#### ISSUED BY: GEOTECHNICAL INSTRUMENTS (UK) LTD

The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor of k=2, providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with UKAS requirements.

Calibrations marked 'Non-UKAS Accredited results' on this certificate have been included for completeness.

#### **Non-UKAS Accredited results:**

Barome	eter (mbar)
Reference	Instrument Reading
1011	1011

Approved by Signatory

Dawn Hemings

Laboratory Inspection

This certificate is issued in accordance with the laboratory accreditation requirements of the United Kingdom Accreditation Service. It provides traceability of measurement to the SI system of units and/or to units of measurement realised at the National Physical Laboratory or other recognised national metrology institutes. This certificate may not be reproduced other than in full, except with the prior written approval of the issuing laboratory.

Page 2 of 2 | LP015GIUKAS-2.2

Geotechnical Instruments (UK) Ltd

Sovereign House, Queensway, Learnington Spa, Warwickshire, CV31 3JR

🞯 geotechuk.com 🙋 service@geotech.co.uk 📘 +44 (0)1926 338111

Geotech

**Instrument Service Report** 

Unit Type: BlOGAS 5000	Part Number:	Date:	Next Sei	Next Service Due:	Customer Name:
Serial Number: G502306	BM5K0000-000	14-Jul-2016	6 13-Jul-2017	17	Fugro Geotechnical Services Ltd
Actions/Investigation Description	ption		Result		Comments
Serial Number Check			Yes		
Full Automatic Calibration			Pass		
Serial Comms Test (USB)			Pass		
Inward Gas Check Performed?			Yes		
Service history of instrument reviewed	ed		Yes		
Inwards gas check data reviewed			Yes		
Instrument turns on			Pass		
Customer specific requirements observed and reported fault(s) acknowledged	served and reported fa	ault(s)	N/A		
Backlight operates correctly			Yes		
External visual inspection performed	q		Pass		
Instrument has latest software			Retest Passed		
Internal visual inspection performed			Pass		
Chemical sensor(s) replaced			N/A		
02 sensor replaced			No		
All screws tightened to correct torque	е		Yes		
All connectors are secure			Pass		

Geotech

Page 1 of 2

Unit Type: BIOGAS 5000	Part Number:	Date:	Next Service Due:	Customer Name:	
Serial Number: G502306	BM5K0000-000	14-Jul-2016	13-Jul-2017	Fugro Geotechnical Services Ltd	s Ltd
<b>Actions/Investigation Description</b>	iption		Result	Comments	
Check diagnostic channels			Pass		
Case compression test			Pass		
Impact and stability test			Pass	×	
Pressure transducer test(s) as per i	as per user operation		Pass		
Final visual inspection on instrument	nt		Pass		27.2
Case assembly closed and screws tightened to correct torque	tightened to correct to	orque	Yes		
Response to customer's reported comments	omments		NA		
PTFE filters replaced			Yes		
Pump flow greater than 550 ml/min			Pass		
Automated instrument pressure system test (leak test)	stem test (leak test)		Pass		
Pump vacuum greater than -400 mb and flow fails	b and flow fails		Pass		
Temperature probe tested			Pass		
Chemical cells calibrated - refer to results on Calibration Certificate	results on Calibration		NA		
Customer Comments					
Returned for full service and calibration.	ation.				
Service Details: Service Scheme		Service Engineer:	Calibration Engineer:		<u>Signature:</u>
Standard Service	<u>≺</u>	Mustafa Ghalaboun	Suk Balrey	Dawn Hemings	£-

**Instrument Service Report** 

Page 2 of 2





# Appendix I

# Landfill Gas Monitoring Results and Graphical Plots



28<sup>th</sup> Monthly Environmental Monitoring and Audit (EM&A) Report – February 2017

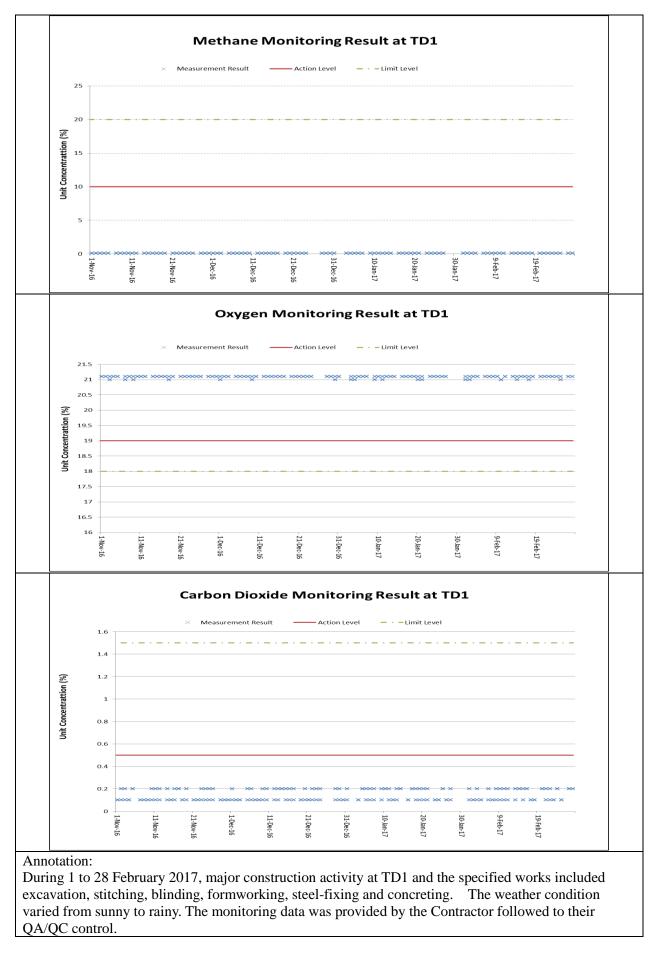

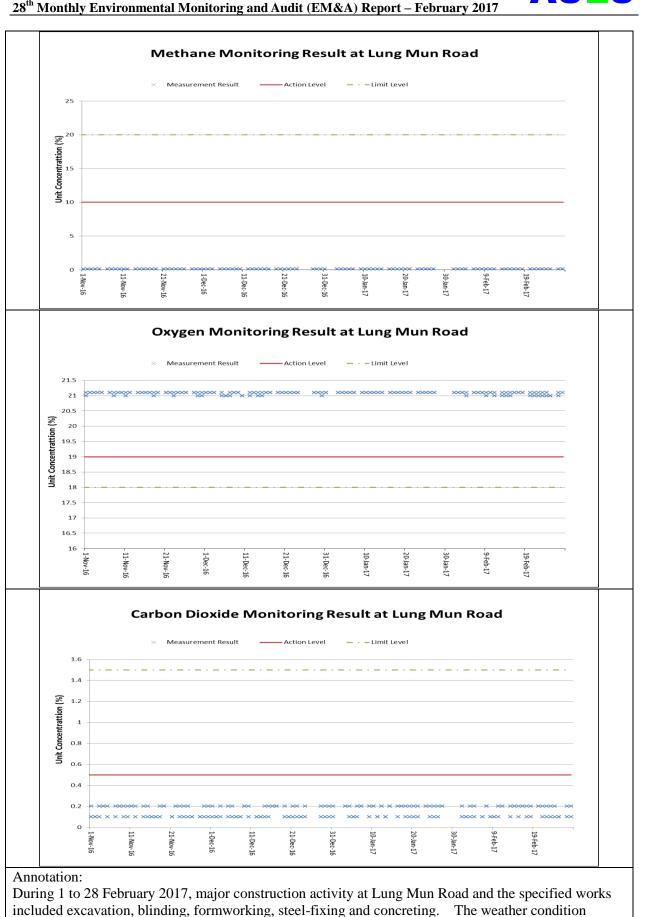

QA/QC control.

varied from sunny to rainy. The monitoring data was provided by the Contractor followed to their



#### Landfill Gas Monitoring Results (TD1)

Monitoring Location	Date				Methane (%)		Oxygen (%)			Carbon Dioxide (%)			
Location	Date	Time	Weather	Temperature (°C)		Action	Limit	Measurement	Action	Limit	Measurement	Action	Limit
					Result	Level	Level	Result	Level	Level	Result	Level	Level
	1/2/2017	8:00	Cloudy	16	0.1	10	20	21.1	19	18	0.1	0.5	1.5
-	1/2/2017	14:00	-	22	0.1	10	20	21.1	19	18	0.1	0.5	1.5
-	2/2/2017 2/2/2017	8:00 14:00	Cloudy	16	0.1	10 10	20 20	21	19 19	18	0.2	0.5	1.5
-	3/2/2017	8:00		18	0.1	10	20	21	19	18	0.1	0.5	1.5
-	3/2/2017	14:00	Fine	20	0.1	10	20	21.1	19	18	0.1	0.5	1.5
F	4/2/2017	8:00		16	0.1	10	20	21.1	19	18	0.2	0.5	1.5
F	4/2/2017	14:00	Cloudy	21	0.1	10	20	21.1	19	18	0.1	0.5	1.5
Ē	6/2/2017	8:00		17	0.1	10	20	21.1	19	18	0.1	0.5	1.5
F	6/2/2017	14:00	Hazy	20	0.1	10	20	21.1	19	18	0.1	0.5	1.5
E E E E E E E E E E E E E E E E E E E	7/2/2017	8:00	Fine	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5
Γ	7/2/2017	14:00	rine	19	0.1	10	20	21.1	19	18	0.1	0.5	1.5
	8/2/2017	8:00	Cloudy	16	0.1	10	20	21.1	19	18	0.1	0.5	1.5
	8/2/2017	14:00	Cloudy	21	0.1	10	20	21.1	19	18	0.2	0.5	1.5
	9/2/2017	8:00	Fine	11	0.1	10	20	21.1	19	18	0.1	0.5	1.5
-	9/2/2017	14:00		17	0.1	10	20	21.1	19	18	0.1	0.5	1.5
-	10/2/2017	8:00	Hazy	11	0.1	10	20	21.1	19	18	0.2	0.5	1.5
L	10/2/2017	14:00	. ,	16	0.1	10	20	21	19	18	0.2	0.5	1.5
-	11/2/2017	8:00	Hazy	11	0.1	10	20	21	19	18	0.1	0.5	1.5
-	11/2/2017	14:00		18	0.1	10	20	21.1	19	18	0.1	0.5	1.5
-	13/2/2017 13/2/2017	8:00 14:00	Sunny	13 20	0.1	10	20	21.1	19	18	0.2	0.5	1.5
	13/2/2017	8:00		16	0.1	10 10	20 20	21.1 21.1	19 19	18	0.1	0.5	1.5
TD1	14/2/2017	14:00	Fine	21	0.1	10	20	21.1	19	18	0.2	0.5	1.5
	15/2/2017	8:00	G	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5
-	15/2/2017	14:00	Sunny	21	0.1	10	20	21.1	19	18	0.2	0.5	1.5
	16/2/2017	8:00		16	0.1	10	20	21.1	19	18	0.2	0.5	1.5
Ē	16/2/2017	14:00	Sunny	24	0.1	10	20	21.1	19	18	0.2	0.5	1.5
F	17/2/2017	8:00	Fine Cloudy	17	0.1	10	20	21.1	19	18	0.2	0.5	1.5
Γ	17/2/2017	14:00		25	0.1	10	20	21	19	18	0.1	0.5	1.5
	18/2/2017	8:00		18	0.1	10	20	21.1	19	18	0.1	0.5	1.5
	18/2/2017	14:00		24	0.1	10	20	21.1	19	18	0.1	0.5	1.5
	20/2/2017	8:00		18	0.1	10	20	21.1	19	18	0.1	0.5	1.5
-	20/2/2017	14:00		25	0.1	10	20	21.1	19	18	0.2	0.5	1.5
L	21/2/2017	8:00	Rain	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5
-	21/2/2017	14:00		21	0.1	10	20	21.1	19	18	0.1	0.5	1.5
-	22/2/2017	8:00	Rain	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5
-	22/2/2017 23/2/2017	14:00		21	0.1	10 10	20	21.1	19	18	0.2	0.5	1.5
-		8:00	Cloudy	15	0.1	-	20	21.1	19	18	0.1	0.5	1.5
ŀ	23/2/2017 24/2/2017	14:00		20	0.1	10	20	21.1	19	18	0.1	0.5	1.5
F		8:00	Fine		0.1	10	20	21.1	19	18	0.1	0.5	1.5
ŀ	24/2/2017	14:00		15	0.1	10	20	21.1	19	18	0.12	0.5	1.5
F	25/2/2017	8:00	Hazy	10	0.1	10	20	21.1	19	18	0.2	0.5	1.5
ŀ	25/2/2017 27/2/2017	14:00 8:00		14	0.1	10 10	20 20	21 21.1	19 19	18	0.1	0.5	1.5
ŀ	27/2/2017	14:00	Fine	20	0.1	10	20	21.1	19	18	0.1	0.5	1.5
ŀ	28/2/2017	8:00		20	0.1	10	20	21.1	19	18	0.2	0.5	1.5
F	28/2/2017	14:00	Hazy	20	0.1	10	20	21.1	19	18		0.5	1.5

 Parameter
 Criteria
 Measurement

 Oxygen
 Action Level
 <19%</td>

 Limit Level
 <18%</td>

 Methane
 Action Level
 >10% LEL (> 0.5% v/v)

 Limit Level
 >20% LEL (>1% v/v)

 Carbon
 Action Level
 >0.5%

 Dioxide
 Limit Level
 >1.5%

					Landfill Gas Monitoring Results (Lung Mun Road) Methane (%) Oxygen (%)						Carbon Dioxide (%)			
Monitoring	Date	Time	Weather	Temperature (°C)		Action	Limit	Measurement	Action	Limit	Measurement	Action	o) Limit	
Location		Thic	weather		Result	Level	Level	Result	Level	Linit Level	Result	Level	Linnt Level	
	1/2/2017	8:20	Cloudy	16	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	1/2/2017	14:20		22	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	2/2/2017	8:20	Cloudy	16	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	2/2/2017	14:20		18	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	3/2/2017	8:20	Fine	15	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	3/2/2017	14:20		20	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	4/2/2017	8:20	Cloudy	16	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	4/2/2017 6/2/2017	14:20 8:20		21 17	0.1	10	20 20	21	19 19	18	0.2	0.5	1.5	
	6/2/2017	14:20	Hazy	20	0.1	10	20	21.1 21.1	19	18	0.1	0.5	1.5	
	7/2/2017	8:20		16	0.1	10	20	21.1 21.1	19	18	0.1	0.5	1.5	
	7/2/2017	14:20	Fine	10	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	8/2/2017	8:20		16	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	8/2/2017	14:20	Cloudy	21	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	9/2/2017	8:20	Ĩ	11	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	9/2/2017	14:20	Fine	17	0.1	10	20	21	19	18	0.1	0.5	1.5	
	10/2/2017	8:20		11	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	10/2/2017	14:20	Hazy	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
Lung Mun Road	11/2/2017	8:20	Hazy	11	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	11/2/2017	14:20	Hazy	18	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	13/2/2017	8:20	Sunny	13	0.1	10	20	21	19	18	0.2	0.5	1.5	
	13/2/2017	14:20	Sumry	20	0.1	10	20	21	19	18	0.1	0.5	1.5	
	14/2/2017	8:20	Fine	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	14/2/2017	14:20	)	21	0.1	10	20	21	19	18	0.2	0.5	1.5	
	15/2/2017	8:20	Sunny	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	15/2/2017	14:20		21	0.1	10	20	21	19	18	0.1	0.5	1.5	
	16/2/2017	8:20	Sunny	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	16/2/2017	14:20	)	24	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	17/2/2017	8:20	Fine	17 25	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	17/2/2017 18/2/2017	14:20		18	0.1	10 10	20 20	21.1	19 19	18	0.2	0.5	1.5	
	18/2/2017	8:20	Fine	24	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	20/2/2017	8:20		18	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	20/2/2017	14:20	Cloudy	25	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	21/2/2017	8:20	)	16	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	21/2/2017	14:20	Rain	21	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	22/2/2017	8:20		16	0.1	10	20	21	19	18	0.1	0.5	1.5	
	22/2/2017	14:20	Rain	21	0.1	10	20	21	19	18	0.2	0.5	1.5	
	23/2/2017	8:20	Claude	15	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	23/2/2017	14:20	Cloudy	20	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	24/2/2017	8:20	Fine	12	0.1	10	20	21	19	18	0.1	0.5	1.5	
	24/2/2017	14:20	THE	15	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
	25/2/2017	8:20	Hazy	10	0.1	10	20	21	19	18	0.1	0.5	1.5	
	25/2/2017	14:20	1102.9	14	0.1	10	20	21	19	18	0.1	0.5	1.5	
	27/2/2017	8:20	Fine	15	0.1	10	20	21	19	18	0.2	0.5	1.5	
	27/2/2017	14:20		20	0.1	10	20	21.1	19	18	0.1	0.5	1.5	
	28/2/2017	8:20	Hazy	16	0.1	10	20	21	19	18	0.2	0.5	1.5	
	28/2/2017	14:20		20	0.1	10	20	21.1	19	18	0.1	0.5	1.5	

#### Landfill Gas Monitoring Results (Lung Mun Road)

Remark:	Parameter	Criteria	Measurement
	Oxygen	Action Level	< 19%
	Oxygen	Limit Level	< 18%
	Methane	Action Level	> 10% LEL (> 0.5% v/v)
	wiethalie	Limit Level	> 20% LEL (>1% v/v)
	Carbon	Action Level	> 0.5%
	Dioxide	Limit Level	> 1.5%



# Appendix J

# **Investigation Report for Exceedance**



(Not Used)



# Appendix K

### **Checklist for Landscape and Visual Monitoring**

#### Contract No. HY/2013/12

Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works



Landscape and Visual Checklist

#### Monitoring Date: <u>3<sup>rd</sup> February 2017</u>

Item	Environmental Protection Measures	Location/ Timing	Implementation		St	atus		Remarks
			Agent	Α	UA	IR	NA	
1	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification,	All areas / During construction	Design Consultant/ Contractor					
	the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage)			√				
2	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme	All areas / During construction	Design Consultant/ Contractor				V	Tree Transplanting Specification has been specified in P.S., no transplantation works has been carried out at this stage.
3	Hillside and roadside screen planting to proposed roads, associated structures and slope works	All areas / During construction	Design Consultant/ Contractor				$\checkmark$	Construction of roads not commenced yet
4	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone)	All areas / During construction	Design Consultant/ Contractor	$\checkmark$				
5	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works	All areas / During construction	Design Consultant/ Contractor			5	$\checkmark$	For some area, erection of hoarding was not feasible due to

						the limitation of traffic sight line; water barrier with panel was used to screen works.
6	Control night-time lighting and glare by hooding all lights	All areas / During construction	Design Consultant/ Contractor	~		Only temporary traffic management lighting was applied.
7	Ensure no run-off into water body adjacent to the Project Area	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		
8	Avoidance of excessive height and bulk of buildings and structures	All areas / During construction	Design Consultant/ Contractor		$\checkmark$	No high-rise building would be constructed.
9	Recycle/Reuse all felled trees and vegetation, e.g. mulching	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		Recycle of trees carried out licensed recycler was conducted.
10	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006	All areas / During construction	Design Consultant/ Contractor		V	Compensatory planting will be carry out in later stage of the project.

Legend: A=Acceptable, UA= Unacceptable, IR=Improvement Required, N/A=Not Applicable

Note: All item reference to Technical Memorandum on Environmental Impact Assessment, TM-CLKL EIA Section 10.9 & Project EM&A Manual Section 7.6

Checked and Monitored by: Chung Koon Wah Albert (RLA) No. R-150 (Date) 3/03/2017

Mes TWTA(ET) 7 Mar Dol7 (Date) Checked by: How Browny (IEC) 10 March 2017 (Date) Checked by:

Page 2/2



Item 1. Existing trees on boundary of the Project Area should be protected carefully during construction.



Item 4. Hydro-seeding or sheeting provided at stockpile.



Item 5. Hoarding with panel around works area & Item 6. Temporary traffic management lighting.



Item 7. Ensure no run-off into water body.




Item 9. Recycle of felled trees as facilities to reuse.

#### Contract No. HY/2013/12

Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works

Landscape and Visual Checklist

#### Monitoring Date: <u>10<sup>th</sup> February 2017</u>

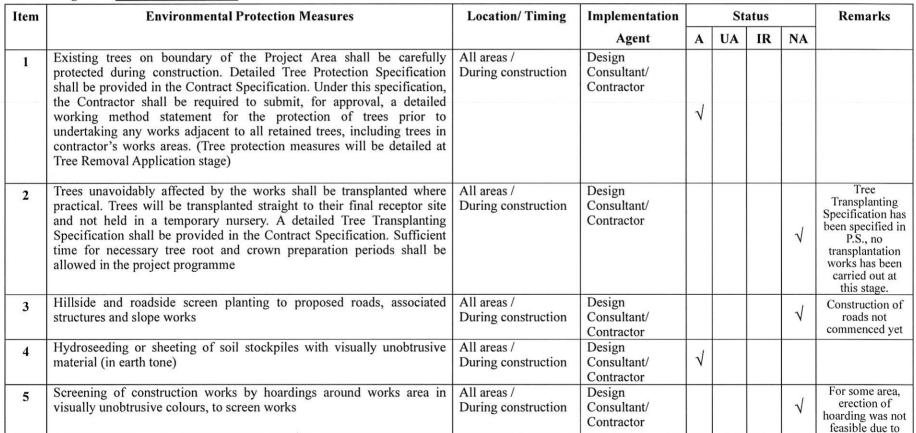



						the limitation of traffic sight line; water barrier with panel was used to screen works.
6	Control night-time lighting and glare by hooding all lights	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		Only temporary traffic management lighting was applied.
7	Ensure no run-off into water body adjacent to the Project Area	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		
8	Avoidance of excessive height and bulk of buildings and structures	All areas / During construction	Design Consultant/ Contractor		1	No high-rise building would be constructed.
9	Recycle/Reuse all felled trees and vegetation, e.g. mulching	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		Recycle of trees carried out licensed recycler was conducted.
10	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006	All areas / During construction	Design Consultant/ Contractor		$\checkmark$	Compensatory planting will be carry out in later stage of the project.

Legend: A=Acceptable, UA= Unacceptable, IR=Improvement Required, N/A=Not Applicable

Note: All item reference to Technical Memorandum on Environmental Impact Assessment, TM-CLKL EIA Section 10.9 & Project EM&A Manual Section 7.6


Checked and Monitored by: Chung Koon Wah Albert (RLA) No. R-150 (Date) 3/03/2017

Checked by: TWTO(ET) 7 May 2017 (Date) Checked by: (IEC) 10 March 2017 (Date)

Page 2/2



Item 1. Existing trees on boundary of the Project Area should be protected carefully during construction.

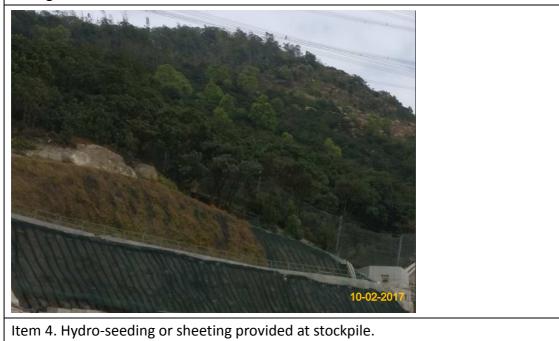



Item 5. Hoarding with panel around works area & Item 6. Temporary traffic management lighting.



Item 7. Ensure no run-off into water body.



Item 9. Recycle of felled trees as facilities to reuse.

#### Contract No. HY/2013/12

Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works



Landscape and Visual Checklist

### Monitoring Date: <u>17<sup>th</sup> February 2017</u>

Item	<b>Environmental Protection Measures</b>	Location/ Timing	Implementation		St	atus		Remarks
			Agent	Α	UA	IR	NA	
1	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed	All areas / During construction	Design Consultant/ Contractor					
	working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage)			N				
2	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme	All areas / During construction	Design Consultant/ Contractor				V	Tree Transplanting Specification has been specified in P.S., no transplantation works has been carried out at this stage.
3	Hillside and roadside screen planting to proposed roads, associated structures and slope works	All areas / During construction	Design Consultant/ Contractor				$\checkmark$	Construction of roads not commenced yet
4	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone)	All areas / During construction	Design Consultant/ Contractor	$\checkmark$				
5	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works	All areas / During construction	Design Consultant/ Contractor				$\checkmark$	For some area, erection of hoarding was not feasible due to

						the limitation of traffic sight line; water barrier with panel was used to screen works.
6	Control night-time lighting and glare by hooding all lights	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		Only temporary traffic management lighting was applied.
7	Ensure no run-off into water body adjacent to the Project Area	All areas / During construction	Design Consultant/ Contractor	$\overline{\mathbf{A}}$		
8	Avoidance of excessive height and bulk of buildings and structures	All areas / During construction	Design Consultant/ Contractor			No high-rise building would be constructed.
9	Recycle/Reuse all felled trees and vegetation, e.g. mulching	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		Recycle of trees carried out licensed recycler was conducted.
10	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006	All areas / During construction	Design Consultant/ Contractor		V	Compensatory planting will be carry out in later stage of the project.

Legend: A=Acceptable, UA= Unacceptable, IR=Improvement Required, N/A=Not Applicable

Note: All item reference to Technical Memorandum on Environmental Impact Assessment, TM-CLKL EIA Section 10.9 & Project EM&A Manual Section 7.6


Checked and Monitored by: Chung Koon Wah Albert (RLA) No. R-150 (Date) 3/03/2017

Checked by: TWTO(ET) 7 May 2017 (Date) The AIEC) 10 March 2017 (Date) Checked by:

Page 2/2




Item 1. Existing trees on boundary of the Project Area should be protected carefully during construction.

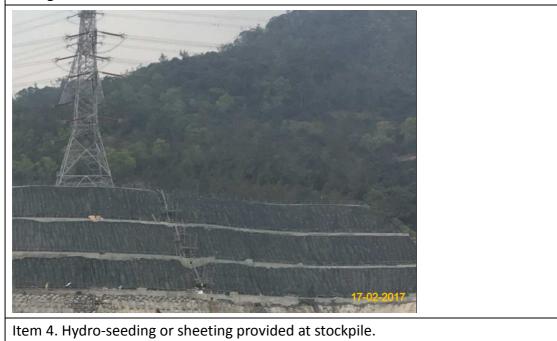



Item 5. Hoarding with panel around works area & Item 6. Temporary traffic management lighting.

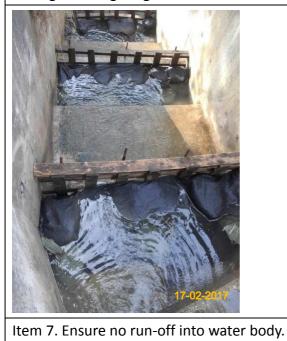



Item 9. Recycle of felled trees as facilities to reuse.

#### Contract No. HY/2013/12

Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works



Landscape and Visual Checklist

### Monitoring Date: <u>24<sup>th</sup> February 2017</u>

Item	Environmental Protection Measures	Location/ Timing	Implementation		St	atus		Remarks
			Agent	A	UA	IR	NA	
1	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification,	All areas / During construction	Design Consultant/ Contractor					
	the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage)			√				
2	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme		Design Consultant/ Contractor				V	Tree Transplanting Specification has been specified in P.S., no transplantation works has been carried out at this stage.
3	Hillside and roadside screen planting to proposed roads, associated structures and slope works	During construction	Design Consultant/ Contractor				$\checkmark$	Construction of roads not commenced yet
4	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone)	All areas / During construction	Design Consultant/ Contractor	$\checkmark$				
5	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works	All areas / During construction	Design Consultant/ Contractor				$\checkmark$	For some area, erection of hoarding was not feasible due to

						the limitation of traffic sight line; water barrier with panel was used to screen works.
6	Control night-time lighting and glare by hooding all lights	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		Only temporary traffic management lighting was applied.
7	Ensure no run-off into water body adjacent to the Project Area	All areas / During construction	Design Consultant/ Contractor	$\checkmark$		
8	Avoidance of excessive height and bulk of buildings and structures	All areas / During construction	Design Consultant/ Contractor		$\checkmark$	No high-rise building would be constructed.
9	Recycle/Reuse all felled trees and vegetation, e.g. mulching	All areas / During construction	Design Consultant/ Contractor	√		Recycle of trees carried out licensed recycler was conducted.
10	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006	All areas / During construction	Design Consultant/ Contractor		V	Compensatory planting will be carry out in later stage of the project.

Legend: A=Acceptable, UA= Unacceptable, IR=Improvement Required, N/A=Not Applicable

Note: All item reference to Technical Memorandum on Environmental Impact Assessment, TM-CLKL EIA Section 10.9 & Project EM&A Manual Section 7.6


Checked and Monitored by: Chung Koon Wah Albert (RLA) No. R-150 (Date) 3/03/2017

Checked by: TWTA(ET) 7 Mar 2017 (Date) - Alen (IEC) 10 March 2017 (Date) Checked by

Page 2/2




Item 1. Existing trees on boundary of the Project Area should be protected carefully during construction.

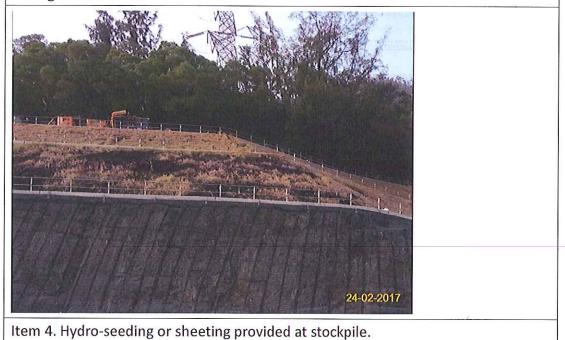



Item 5. Hoarding with panel around works area & Item 6. Temporary traffic management lighting.

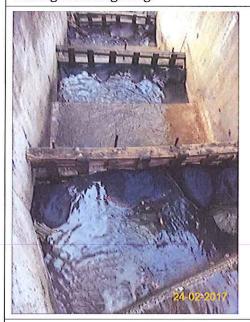

Item 7. Ensure no run-off into water body.





# Appendix L

### **Monthly Summary Waste Flow Table**

#### Appendix A – Monthly Waste Flow Table

		Annual Quanti	ties of Inert C8	D Materials Ge	nerated Month	ly	Ann	ual Quantities o	of C&D Wastes	Generated Mor	nthly.
Month	Total Quantity Generated	Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals (see note 4)	Paper / cardboard packaging (see note 4)	Plastics & Rubber (see note 2)	Chemical Waste	Others (general refuse)
	(in `000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in `000m <sup>3</sup> )	(in `000m <sup>3</sup> )	(in `000m <sup>3</sup> )	(in `000m <sup>3</sup> )	(in `000kg)	(in `000kg)	(in `000kg)	(in `000kg)	(in `000m <sup>3</sup> )
Jan	13.117	0.000	4.543	7.512	1.062	0.000	0.000	0.000	0.000	0.000	0.217
Feb	14.249	0.000	1.066	10.617	2.566	0	0.000	0.000	0.000	0.000	0.074
Mar											
Apr											
Мау											
June											
Sub-total	27.366	0.000	5.609	18.129	3.628	0.000	0.000	0.000	0.000	0.000	0.291
July											
Aug											
Sept											
Oct											
Nov											
Dec											
Total	27.366	0.000	5.609	18.129	3.628	0.000	0.000	0.000	0.000	0.000	0.291

#### Monthly Summary Waste Flow Table for 2017 (year)

Notes:

1 The waste flow table shall also include C&D materials that are specified in the contract to be imported for use at the Site.

2 Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.

3 Broken concrete for recycling into aggregates.



# Appendix M

### **Environmental Mitigation and Enhancement Measures Implementation Schedule (EMIS)**

Air Quali EIA	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation	Relevant Standard or	Implementation Stages			Status *
reference	reference	Environmental i rotection measures	Location/ Thining	Agent	Requirement	D	C	0	Status
4.8.1	3.8	An effective watering programme of twice daily watering with complete coverage, is estimated to reduce by 50%. This is recommended for all areas in order to reduce dust levels to a minimum;	All areas / throughout construction period	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		$\checkmark$
4.8.1	3.8	Watering of the construction sites in Lantau for 8 times/day and in Tuen Mun for 12 times/day to reduce dust emissions by 87.5% and 91.7% respectively and shall be undertaken.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		$\checkmark$
4.8.1	3.8	The Contractor shall, to the satisfaction of the Engineer, install effective dust suppression measures and take such other measures as may be necessary to ensure that at the Site boundary and any nearby sensitive receiver, dust levels are kept to acceptable levels.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		~
4.8.1	3.8	The Contractor shall not burn debris or other materials on the works areas.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		$\checkmark$
4.8.1	3.8	In hot, dry or windy weather, the watering programme shall maintain all exposed road surfaces and dust sources wet.	All unpaved haul roads / throughout construction period in hot, dry or windy weather	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		<>
4.8.1	3.8	Where breaking of oversize rock/concrete is required, watering shall be implemented to control dust. Water spray shall be used during the handling of fill material at the site and at active cuts, excavation and fill sites where dust is likely to be created.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		<>
4.8.1	3.8	Open dropping heights for excavated materials shall be controlled to a maximum height of 2m to minimise the fugitive dust arising from unloading.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		$\checkmark$

reference	reference		Location, Thinking	Agent	Requirement	D	C	0	Status
EIA	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation	Relevant Standard or	Imp	lement Stages		Status
Ecology									
11.8	Section 9	EM&A in the form of audit of the mitigation measures	All areas / throughout construction period	Highways Department	EIAO-TM		Y		$\checkmark$
EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	D	Stages C		Status
Cultural	-			Γ		Imm	lement	tion	
		dust monitoring and site audit	ASRs / throughout construction period		Manual				
4.11	Section 3	in dry or windy condition. EM&A in the form of 1 hour and 24 hour	All representative existing	Contractor	generation EM&A		Y		$\checkmark$
4.8.1	3.8	All stockpiles of aggregate or spoil shall be enclosed or covered and water applied	All areas / throughout construction period	Contractor	TMEIA Avoid dust		Y		$\checkmark$
4.8.1	3.8	Areas of exposed soil shall be minimized to areas in which works have been completed shall be restored as soon as is practicable.	All exposed surfaces / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		$\checkmark$
4.8.1	3.8	No earth, mud, debris, dust and the like shall be deposited on public roads. Wheel washing facility shall be usable prior to any earthworks excavation activity on the site.	construction period	Contractor	TMEIA Avoid dust generation		Y		$\checkmark$
4.8.1	3.8	Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		V
4.8.1	3.8	During transportation by truck, materials shall not be loaded to a level higher than the side and tail boards, and shall be dampened or covered before transport.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		$\checkmark$

14.12.2	1	Safety Measures - Excavation	Construction Stage	Contractor	EPD/TR8/97 -		Y		$\checkmark$
17.12.2	17.2	Appoint a properly trained safety officer and provide with appropriate equipment to measure and monitor LFG hazard. The monitoring frequency and areas to be monitored should be set down prior to commencement of ground-works either by the Safety Officer or an approved and appropriately qualified person.	Construction Stage		Landfill Gas Hazard Assessment Guidance Note				
14.12.2	14.2	Appointment of Safety Officer	Construction Stage	Contractor	EPD/TR8/97 -		Y Y	~	$\checkmark$
EIA reference	EM&A Manual reference	<b>Environmental Protection Measures</b>	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp D	lement Stages C	ation O	Status
Landfill (	Gas Hazaro	Assessment				-			
7.13	6.5	Construction activities should be restricted to the proposed works boundary	All areas / Throughout construction	Contractor	TMEIA		Y		$\checkmark$
7.13	6.5	Disturbed areas to be reinstated immediately after completion of the works.	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Placement of equipment in designated areas within the existing disturbed land	All areas / Throughout construction period	Contractor	TMEIA		Y		$\checkmark$
7.13	6.5	Avoid damage and disturbance to the remaining and surrounding natural habitat	All areas / Throughout construction period	Contractor	TMEIA		Y		$\checkmark$
7.13	6.5	Spoil heaps shall be covered at all times.	All areas / Throughout construction period	Contractor	TMEIA		Y		$\checkmark$
7.13	6.5	The loss of habitat shall be supplemented by enhancement planting in accordance with the landscape mitigation schedule.	All areas / As soon as accessible	Contractor	TMEIA		Y		$\checkmark$
7.13	6.5	Audit Pitcher Plant protection measures	Tuen Mun Area 46	Contractor	TMEIA		Y		$\checkmark$
7.13#	6.3, 6.5#	Fencing or other physical barriers for protection of Pitcher Plant around Zones 8, 9 and 10 and the temporary nursery site	Tuen Mun Area 46 shrubland/ Detailed/ Prior to construction	Design Consultant/ Contractor	TMEIA	Y	Y		$\checkmark$

14.12.2	-	Staff should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards. Excavation procedures and code of practice should be implemented.Safety Measures – Welding, Flame- Cutting and Hot worksHot works should be confined to open areas away from any trench or excavation. Should hot works	Construction Stage	Contractor	Landfill Gas Hazard Assessment Guidance Note EPD/TR8/97 - Landfill Gas Hazard Assessment	Y	√
14.12.2	-	must be carried out in trenches or confined space, "permit to work" procedures should be followed. <u>Safety Measures – Enclosed Spaces</u> Site offices or buildings located within PPV Landfill Consultation Zone which have the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas; or be raised clear of the ground by a	Site office, building, tunnel, subway, confined area / Construction Stage	Contractor	Guidance Note EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note	Y	
14.12.2	-	Software in the second of the ground by a minimum of 500mm.         Safety Measures – Electrical Equipment         Any electrical equipment, such as motors and extension cords, should be intrinsically safe.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note	Y	
14.12.2	-	<u>Safety Measures – Piping</u> During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed as installed to prevent the migration of gases through the pipeline/conduit. All piping/conduiting should be capped at the end of each working day.	Services & utilities / Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note	Y	✓
14.12.2	-	<u>Safety Measures – Fire Safety</u> Adequate fire safety equipments should be provided on site. Workers and visitors should be notified of the potential fire hazards. Safety notices should be	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment	Y	

		posted around the site warning the anger and potential hazards.			Guidance Note		
14.12.1	-	<u>Safety Measures – Confined Spaces</u> Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces, and that appropriate monitoring procedures are in place to prevent hazards in confined spaces.	Confined space / Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note	Y	$\checkmark$
14.12.1	-	<u>Monitoring</u> Periodically during ground-works within the Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. Depending on the results of the measurements, actions required will vary. As a minimum these should encompass those actions specified in Table 14.8 of the EIA Report or Table 14.1 of the EM&A Manual.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note	Y	✓
Landscap	he and Visu	ลไ					
	EM&A			<b>T I ( /</b> )	Relevant	lement	
EIA reference		Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	lement Stages C	Status
	EM&A Manual		Location/ Timing All areas/detailed design/ during construction		Standard or	 Stages	Status

		transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme (CM2)	construction	Contractor		V	V		NA
10.9	7.6	Hillside and roadside screen planting to proposed roads, associated structures and slope works (CM3)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y		NA
10.9	7.6	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone) (CM4)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y		$\checkmark$
10.9	7.6	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works (CM5)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		< >
10.9	7.6	Control night-time lighting and glare by hooding all lights (CM6)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		$\checkmark$
10.9	7.6	Ensure no run-off into water body adjacent to the Project Area (CM7)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		$\checkmark$
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (CM8)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		$\checkmark$
10.9	7.6	Recycle/Reuse all felled trees and vegetation, e.g. mulching (CM9)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		$\checkmark$
10.9	7.6	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006 (CM10)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		NA
10.9	7.6	Re-vegetation of affected woodland/shrubland with	All areas/detailed design/	Design	TMEIA	Y	Y	Y	N/A

		native species (OM1)	during Construction/ post construction	Consultant/ Contractor					
10.9	7.6	Tall buffer screen tree / shrub / climber planting where appropriate should be incorporated to soften hard engineering structures and facilities (OM2)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Streetscape elements (e.g. paving, signage, street furniture, lighting etc.) shall be sensitively designed in a manner that responds to the local context, and minimises potential negative landscape and visual impacts. Lighting units should be directional and minimize unnecessary light spill (OM3)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Structure, ornamental tree / shrub / climber planting should be provided along roadside amenity strips, central dividers and newly formed slopes to enhance the townscape quality and further greenery enhancement (OM4)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Aesthetically pleasing design (visually unobtrusive and non-reflective) as regard to the form, material and finishes shall be incorporated to all buildings, engineering structures and associated infrastructure facilities (OM5)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (OM6)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	$\checkmark$
Waste									
EIA	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation	Relevant Standard or	Imp	Implementation Stages		Status
reference	reference		8	Agent	Requirement	D	С	0	
12.6		The Contractor shall identify a coordinator for the management of waste.	Contract mobilisation	Contractor	TMEIA		Y		√ 
12.6		The Contractor shall prepare and implement a Waste Management Plan which specifies procedures such	Contract mobilisation	Contractor	TMEIA, Works Branch		Y		$\checkmark$

		as a ticketing system, to facilitate tracking of loads and to ensure that illegal disposal of wastes does not occur, and protocols for the maintenance of records of the quantities of wastes generated, recycled and disposed. A recording system for the amount of waste generated, recycled and disposed (locations) should be established.			Technical Circular No. 5/99 for the Trip-ticket System for Disposal of Construction and Demolition Material		
12.6		The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges.	Contract mobilisation	Contractor	TMEIA, Land (Miscellaneou s Provisions) Ordinance (Cap 28); Waste Disposal Ordinance (Cap 354); Dumping at Sea Ordinance (Cap 466); Water Pollution Control Ordinance.	Y	~
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedures including waste reduction, reuse and recycling	Contract mobilisation	Contractor	TMEIA	Y	$\checkmark$
12.6	8.1	The extent of cutting operation should be optimised where possible. Earth retaining structures and bored pile walls should be proposed to minimize the extent of cutting.	All areas / throughout construction period	Contractor	TMEIA	Y	~

12.6	8.1	Inert C&D materials from the toll plaza cut slopes shall be reused for construction of the raised platform for the toll plaza where possible.	Tol Plaza / toll plaza construction period	Contractor	TMEIA	Y	~
12.6	8.1	The site and surroundings shall be kept tidy and litter free.	All areas / throughout construction period	Contractor	TMEIA	Y	✓
12.6	8.1	No waste shall be burnt on site.	All areas / throughout construction period	Contractor	TMEIA	Y	~
12.6	8.1	The Contractor shall be prohibited from disposing of C&D materials at any sensitive locations. The Contractor should propose the final disposal sites in the EMP and WMP for approval before implementation.	All areas / throughout construction period	Contractor	TMEIA	Y	✓
12.6	8.1	Stockpiled material shall be covered by tarpaulin and /or watered as appropriate to prevent windblown dust/ surface run off.	All areas / throughout construction period	Contractor	TMEIA	Y	$\diamond$
12.6	8.1	Excavated material in trucks shall be covered by tarpaulins to reduce the potential for spillage and dust generation.	All areas / throughout construction period	Contractor	TMEIA	Y	✓
12.6	8.1	Wheel washing facilities shall be used by all trucks leaving the site to prevent transfer of mud onto public roads.	All areas / throughout construction period	Contractor	TMEIA	Y	✓
12.6	8.1	Standard formwork or pre-fabrication should be used as far as practicable so as to minimise the C&D materials arising. The use of more durable formwork/ plastic facing for construction works should be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should avoid over-ordering and wastage.	All areas / throughout construction period	Contractor	TMEIA	Y	✓
12.6	8.1	<ul> <li>The Contractor should recycle as many C&amp;D materials (this is a waste section) as possible on-site.</li> <li>The public fill and C&amp;D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper</li> </ul>	All areas / throughout construction period	Contractor	TMEIA	Y	

12.6	8.1	disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials.Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.All falsework will be steel instead of wood.	All areas / throughout construction period	Contractor	TMEIA	Y	
12.6	8.1	<ul> <li>Chemical waste producers should register with the EPD. Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows:</li> <li>suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed;</li> <li>Having a capacity of &lt;450L unless the specifications have been approved by the EPD; and</li> <li>Displaying a label in English and Chinese according to the instructions prescribed in Schedule 2 of the Regulations.</li> <li>Clearly labelled and used solely for the storage of chemical wastes;</li> <li>Enclosed with at least 3 sides;</li> <li>Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest;</li> <li>Adequate ventilation;</li> <li>Sufficiently covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and</li> </ul>	All areas / throughout construction period	Contractor	TMEIA	Y	
		Incompatible materials are adequately separated.		~		v	
12.6	8.1	Waste oils, chemicals or solvents shall not be	All areas / throughout	Contractor	TMEIA	Y	v

reference	reference		Liocution, Thinking	Agent	Requirement	D	С	0	Status
EIA	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation	Relevant Standard or		ementa Stages		Status
Water Qu	uality								
12.6	Section 8	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.	All areas / throughout construction period	Contractor	EM&A Manual		Y		✓
12.6	8.1	Office wastes can be reduced by recycling of paper if such volume is sufficiently large to warrant collection. Participation in a local collection scheme by the Contractor should be advocated. Waste separation facilities for paper, aluminum cans, plastic bottles, etc should be provided on-site.	Site Offices/ throughout construction period	Contractor	TMEIA		Y		✓ 
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including waste reduction, reuse and recycling.	All areas / throughout construction period	Contractor	TMEIA		Y		$\checkmark$
12.6	8.1	All waste containers shall be in a secure area on hardstanding;	All areas / throughout construction period	Contractor	TMEIA		Y		<i>√</i>
12.6	8.1	<ul> <li>be maintained in reasonable states, which will not deter the workers from utilising them.</li> <li>Night soil should be regularly collected by licensed collectors.</li> <li>General refuse arising on-site should be stored in enclosed bins or compaction units separately from C&amp;D and chemical wastes. Sufficient dustbins shall be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station. Burning of refuse on construction sites is prohibited.</li> </ul>	All areas / throughout construction period All areas / throughout construction period	Contractor Contractor	TMEIA		Y		✓ ✓
12.6	8.1	disposed of to drain, Adequate numbers of portable toilets should be provided for on-site workers. Portable toilets should	construction period All areas / throughout construction period	Contractor	TMEIA		Y		$\checkmark$

Land Wo	orks						
6.10	-	Wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	
6.10	-	Sewage effluent and discharges from onsite kitchen facilities shall be directed to Government sewer in accordance with the Requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	V
6.10	-	Storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	$\checkmark$
6.10	-	Silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	✓
6.10	-	Temporary access roads should be surfaced with crushed stone or gravel.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	$\diamond$
6.10	-	Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	
6.10	-	Measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	~
6.10	-	Open stockpiles of construction materials (e.g. aggregates and sand) on site should be covered with tarpaulin or similar fabric during rainstorms.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	$\diamond$
6.10	5.8	Manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction	All areas/ throughout construction period	Contractor	TM-EIAO	Y	$\diamond$

6.10		<ul> <li>materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers.</li> <li>Discharges of surface run-off into foul</li> </ul>		Contractor	TM-EIAO		
0.10	-	sewers must always be prevented in order not to unduly overload the foul sewerage system.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	
6.10	-	All vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	~
6.10	-	Section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	✓
6.10	-	Wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	~
6.10	-	Vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for off site disposal.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	~
6.10	-	The Contractor shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	✓
6.10	-	Waste oil should be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance.	All areas/ throughout construction period	Contractor	TM-EIAO Waste Disposal Ordinance	Y	√ 
6.10	-	All fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank.	All areas/ throughout construction period	Contractor	TM-EIAO	Y	\$

6.10	Section 5	All construction works shall be subject to routine audit to ensure implementation of all EIA	All areas/ throughout	Contractor	EM&A Manual	Y	$\checkmark$
		recommendations and good working practice.	construction period				

Remarks:

- ✓ Compliance of Mitigation Measures
- <> Compliance of Mitigation Measures but need improvement.
- × Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Contractor
- $\triangle$  Deficiency of Mitigation Measures but rectified by Contractor
- N/A Not Applicable in Reporting Period
- # Amended against condition 3.13 of EP-354/2009/C

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government



# Appendix N

### **Cumulative Statistics on Exceedance and Complaint**



Departing	Environmental	Environmontal	Ev	ent Exceedance
Reporting Period	Aspect / Parameter	Environmental Performance	Reporting Period	Cumulative since project commencement
	Air Quality –	Action Level	0	4
February	1-hour TSP	Limit Level	0	0
2017	Air Quality –	Action Level	0	0
	24-hour TSP	Limit Level	0	0

 Table N-1
 Statistical Summary of Environmental Exceedance

#### Table N-2 Statistical Summary of Environmental Complaints

		Environmental Complaint Statistics									
Reporting Period	Ene en en en	Complaint Nature		Complaint Natu		C L Comp		<b>Complaint Nature</b>		Complaint Nature	
	Frequency	Cumulative	Air	Water							
February 2017	0	7	1	NA	6						
Cumulative since	7	7	1	NA	6						
project commencement	1	1	1	INA	U						

 Table N-3
 Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics					
	Frequency	Cumulative	Complaint Nature			
			Air	Noise	Water	
February 2017	0	0	NA	NA	NA	
Cumulative since project commencement	0	0	NA	NA	NA	

#### Table N-4 Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics					
	Frequency	Cumulative	Complaint Nature			
			Air	Noise	Water	
February 2017	0	0	NA	NA	NA	
Cumulative since project commencement	0	0	NA	NA	NA	



# Appendix O

### **Investigation Report for the Complaint**



(Not Used)



# Appendix P

# Inspection Checklist for Vulnerable to Contaminated Water Discharge



(Not Used)
