

**Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link –
Northern Connection Tunnel
Buildings, Electrical and Mechanical
Works**

Thirteenth Monthly EM&A Report

12 July 2019

Environmental Resources Management
2507, 25/F One Harbourfront
18 Tak Fung Street
Hung Hom, Kowloon
Hong Kong
Telephone 2271 3000
Facsimile 2723 5660





Contract No. HY/2017/10 Tuen Mun – Chek Lap Kok Link – Northern Connection Tunnel Buildings, Electrical and Mechanical Works

**Environmental Resources
Management**

2507, 25/F One Harbourfront
18 Tak Fung Street
Hung Hom, Kowloon
Hong Kong
Telephone: (852) 2271 3000
Facsimile: (852) 2723 5660
E-mail: post.hk@erm.com
http://www.erm.com

Thirteenth Monthly EM&A Report

Document Code: 0463091_13th Monthly EM&A_20190712.doc

Client: Gammon		Project No: 0463091			
Summary: This document presents the Thirteenth Monthly EM&A Report for Tuen Mun – Chek Lap Kok Link – Northern Connection Tunnel Buildings, Electrical and Mechanical Works.		Date: 12 July 2019			
		Approved by: 			
		<i>Mr Craig Reid</i> Partner			
		Certified by: 			
		<i>Dr Jasmine Ng</i> ET Leader			
	Thirteenth Monthly EM&A Report	CY	JN	CAR	12/7/19
Revision	Description	By	Checked	Approved	Date
<p>This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client.</p> <p>We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.</p>		<p>Distribution</p> <p><input type="checkbox"/> Internal</p> <p><input checked="" type="checkbox"/> Public</p> <p><input type="checkbox"/> Confidential</p>			
		 			

12 July 2019

By Fax (2783 0155) and By Post

AECOM Asia Company Limited
Supervising Officer's Representative Office
No. 8 Mong Fat Street, Tuen Mun, New Territories, Hong Kong

Attention: Mr. Desmond Fung

Dear Mr. Fung,

**Re: Agreement No. CE 48/2011 (EP)
Environmental Project Office for the
HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing Facilities, and
Tuen Mun-Chek Lap Kok Link – Investigation**

**Contract No. HY/2017/10
TM-CLKL – Northern Connection Tunnel Buildings, E&M Works
13th Monthly EM&A Report for June 2019**

Reference is made to the Environmental Team's submission of the monthly EM&A report for June 2019 (ET's ref.: "0463091_13th Monthly EM&A_20190712.doc" dated 12 July 2019) certified by the ET Leader and provided to us via e-mail on 12 July 2019.

Please be informed that we have no adverse comments on the captioned submission. We write to verify the captioned submission in accordance with Condition 4.4 of EP-354/2009/D.

Thank you for very much your attention. Please feel free to contact the undersigned or the ENPO Leader, Mr. Y H Hui, should you require further information.

Yours sincerely,
For and on behalf of
Ramboll Hong Kong Limited



F. C. Tsang
Independent Environmental Checker
Tuen Mun-Chek Lap Kok Link

c.c.

HyD	Mr. Patrick Ng	(By Fax: 3188 6614)
HyD	Mr. Cheng Pan	(By Fax: 3188 6614)
AECOM	Mr. Conrad Ng	(By Fax: 3922 9797)
ERM	Dr. Jasmine Ng	(By Fax: 2723 5660)
Gammon	Mr. Max Poon	(By Fax: 3520 0486)

Internal: DY, YH, RY, DF, HW, ENPO Site

Q:\Projects\HYDHZMBEEM00\02_Proj_Mgt\02_Corr\HYDHZMBEEM00_0_7518L.19.doc

TABLE OF CONTENTS

	EXECUTIVE SUMMARY	I
1	INTRODUCTION	1
1.1	BACKGROUND	1
1.2	SCOPE OF REPORT	2
1.3	ORGANIZATION STRUCTURE	2
1.4	SUMMARY OF CONSTRUCTION WORKS	2
2	EM&A RESULTS	4
2.1	AIR QUALITY	4
2.2	LANDFILL GAS HAZARD MONITORING	5
2.3	EM&A SITE INSPECTION	5
2.4	WASTE MANAGEMENT STATUS	6
2.5	ENVIRONMENTAL LICENSES AND PERMITS	7
2.6	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	9
2.7	SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMANCE LIMIT	9
2.8	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS	9
3	FUTURE KEY ISSUES	10
3.1	CONSTRUCTION ACTIVITIES FOR THE COMING MONTH	10
3.2	KEY ISSUES FOR THE COMING MONTH	10
4	CONCLUSIONS AND RECOMMENDATIONS	11
4.1	CONCLUSIONS	11

List of Appendices

- Appendix A Project Organization for Environmental Works
- Appendix B Construction Programmes
- Appendix C Implementation Schedule of Environmental Mitigation Measures (EMIS)
- Appendix D Summary of Action and Limit Levels
- Appendix E Event Action Plan
- Appendix F Monthly Summary of Waste Flow Table
- Appendix G Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

EXECUTIVE SUMMARY

Under *Contract No. HY/2017/10*, Gammon Construction Limited (GCL) is commissioned by the Highways Department (HyD) to undertake Northern Connection Tunnel Buildings, Electrical and Mechanical Works of the Tuen Mun – Chek Lap Kok Link Project (TM-CLK Link Project) while AECOM Asia Company Limited was appointed by HyD as the Engineer. For implementation of the environmental monitoring and audit (EM&A) programme under the Contract, ERM-Hong Kong, Limited (ERM) has been appointed as the Environmental Team (ET) in accordance with *Environmental Permit No. EP-354/2009/A*. Ramboll Hong Kong Ltd. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO). Subsequent applications for variation of environmental permits (VEP), *EP-354/2009/B*, *EP-354/2009/C* and *EP-354/2009/D*, were granted on 28 January 2014, 10 December 2014 and 13 March 2015, respectively.

The construction phase of the Contract commenced on 7 June 2018 and will tentatively be completed by 2021. The impact monitoring of the EM&A programme, including air quality and environmental site inspections, were commenced on 7 June 2018.

This is the thirteenth Monthly EM&A report presenting the EM&A works carried out during the period from 1 to 30 June 2019 for the *Contract No. HY/2017/10 Northern Connection Tunnel Buildings, Electrical and Mechanical Works* (the “Contract”) in accordance with the Updated EM&A Manual of the TM-CLK Link Project. As informed by the Contractor, major activities in the reporting period included:

Land-based Works

- Electrical and Mechanical Works and Architectural Builders Work and Finishes at Toll Control Building;
- Electrical and Mechanical Works at Ventilation Plant Room;
- Electrical and Mechanical Works at North Ventilation Building;
- Building Structure at Administration Building;
- Building Structure at Maintenance Depot;
- Building structure at Fire Services Department Building;
- Building Structure at Customs and Excise Department Building;
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Kiosk N2; and
- Electrical and Mechanical Works at the Tunnel;

- Electrical and Mechanical Works and Architectural Builders Work and Finishes at underpass at C3 area; and
- Building Structure at Satellite Control Buil

A summary of monitoring and audit activities conducted in the reporting period is listed below ⁽¹⁾:

24-hour TSP Monitoring	10 sessions
1-hour TSP Monitoring	10 sessions
Joint Environmental Site Inspection	4 sessions

Summary of Breaches of Action/Limit Levels

Breaches of Action and Limit Levels for Air Quality

No exceedance of Action and Limit Levels of 1-hour TSP and 24-hour TSP was recorded by the Environmental Team of Contract No. HY/2012/08 during the reporting period.

Breaches of Action and Limit Levels for Landfill Gas Hazard Monitoring

No exceedance of Action and Limit Levels was recorded for landfill gas hazard monitoring in the reporting month as landfill gas hazard monitoring was temporarily suspended in June 2019.

Environmental Complaints, Non-compliance & Summons

There was no environmental complaint, notification of summons or successful prosecution recorded in the reporting period.

Reporting Change

There was no reporting change in the reporting period.

Upcoming Works for the Next Reporting Month

Works to be undertaken in the next monitoring period of July 2019 include the following:

Land-based Works

- Electrical and Mechanical Works and Architectural Builders Work and Finishes at Toll Control Building;
- Electrical and Mechanical Works at Ventilation Plant Room;
- Electrical and Mechanical Works at North Ventilation Building;

(1) ET justification on the Contract Specific Environmental Monitoring and Audit activities under this Contract was submitted to ENPO on 11 September 2018

- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Administration Building;
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Maintenance Depot;
- Building structure at Fire Services Department Building;
- Building Structure at Customs and Excise Department Building;
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Kiosk N2; and
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at the Tunnel;
- Electrical and Mechanical Works and Architectural Builders Work and Finishes at underpass at C3 area; and
- Building Structure at Satellite Control Building.

Future Key Issues

Potential environmental impacts arising from the above upcoming construction activities in the next reporting month of July 2019 are mainly associated with dust and waste management issues.

1.1

BACKGROUND

According to the findings of the Northwest New Territories (NWNT) Traffic and Infrastructure Review conducted by the Transport Department, Tuen Mun Road, Ting Kau Bridge, Lantau Link and North Lantau Highway would be operating beyond capacity after 2016. This forecast has been based on the estimated increase in cross boundary traffic, developments in the Northwest New Territories (NWNT), and possible developments in North Lantau, including the Airport developments, the Lantau Logistics Park (LLP) and the Hong Kong – Zhuhai – Macao Bridge (HZMB). In order to cope with the anticipated traffic demand, two new road sections between NWNT and North Lantau – Tuen Mun – Chek Lap Kok Link (TM-CLKL) and Tuen Mun Western Bypass (TMWB) are proposed.

An Environmental Impact Assessment (EIA) of TM-CLKL (the Project) was prepared in accordance with the EIA Study Brief (No. ESB-175/2007) and the *Technical Memorandum of the Environmental Impact Assessment Process (EIAO-TM)*. The EIA Report was submitted under the Environmental Impact Assessment Ordinance (EIAO) in August 2009. Subsequent to the approval of the EIA Report (EIAO Register Number AEIAR-146/2009), an Environmental Permit (EP-354/2009) for TM-CLKL was granted by the Director of Environmental Protection (DEP) on 4 November 2009, and EP variation (VEP) (EP-354/2009/A) was issued on 8 December 2010. Subsequent applications for variation of environmental permits (VEPs), EP-354/2009/B, EP-354/2009/C and EP-354/2009/D, were granted on 28 January 2014, 10 December 2014 and 13 March 2015, respectively.

Under *Contract No. HY/2017/10*, Gammon Construction Limited (GCL) is commissioned by the Highways Department (HyD) to undertake the Northern Connection Tunnel Buildings, Electrical and Mechanical Works of TM-CLKL while AECOM Asia Company Limited was appointed by HyD as the Engineer. For implementation of the environmental monitoring and audit (EM&A) programme under the Contract, ERM-Hong Kong, Limited (ERM) has been appointed as the Environmental Team (ET). Ramboll Hong Kong Ltd. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO).

The construction phase of the Contract commenced on 7 June 2018 and will be tentatively completed by 2021. The impact monitoring phase of the EM&A programme, including air quality and environmental site inspections, commenced on 7 June 2018.

The general layout plan of the Contract components is presented in *Figures 1.1 & 1.2a to c*.

Project Management Initials: Designer: KATH Checked: SYLC Approved: CWN ISO A1 594mm x 841mm

Plot File by: jerrywong 23-Jan-18
 PATH: Y:\TO\RSS\MSL\C4 Drawings\C4_Drawing (2018_01_02)\A-architectural drawings -CON\60240249_C4_7051.dgn



AECOM

PROJECT
 TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE
 TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TUNNEL BUILDINGS, ELECTRICAL AND MECHANICAL WORKS

CLIENT
 路政署 HIGHWAYS DEPARTMENT
 港珠澳大橋香港工程管理有限公司 Hong Kong - Zhuhai - Macao Bridge Hong Kong Project Management Office

CONSULTANT
 AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS

Figure 1.1

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK.
A	JAN.18	TENDER ADDENDUM NO.1	SYLC
-	DEC.17	TENDER DRAWING	SYLC

STATUS

SCALE
 A1 1:40000

DIMENSION UNIT
 MILLIMETRES

KEY PLAN

PROJECT NO.
 60240249

CONTRACT NO.
 HY/2017/10

SHEET TITLE
 OVERALL SITE PLAN

SHEET NUMBER
 60240249/C4/7051A

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Plot File by: Jerry Wong 23-Jan-18
 PATH: Y:\TOTO\RES\SUB\1\CA Drawings\CA Drawing (2018_01_02)\Architectural drawings - CON\60240249 CA_7061.dgn
 Project Management Initials: Designer: WATH Chenweid SYLC Approved: CWN ISO 1194mm x 847mm
 01/7071 01/7072



AECOM

PROJECT
1.3

TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE
TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TUNNEL BUILDINGS, ELECTRICAL AND MECHANICAL WORKS

CLIENT

HIGHWAYS DEPARTMENT
 路政署
 香港 - 珠海 - 澳門大橋
 Hong Kong - Zhuhai - Macao Bridge
 Hong Kong Project Management Office

CONSULTANT

AECOM
 AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS

NET ENGINEERING

Figure 1.2a

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK.
A	JAN.18	TENDER ADDENDUM NO.1	SYLC
-	DEC.17	TENDER DRAWING	SYLC

STATUS

SCALE: 1:2500
DIMENSION UNIT: MILLIMETRES

KEY PLAN

PROJECT NO. 60240249
CONTRACT NO. HY/2017/10

SHEET TITLE
ZONING PLAN (SHEET 1)

SHEET NUMBER
60240249/C4/7061A

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as signed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale the document. All measurements must be obtained from the stated dimensions.

Project Management initials: Designer: KATH Checked: SYLC Approved: CWN ISO A1 394mm x 641mm

Plot File by: Jerry Wong 15-Jan-16
 PATH: Y:\TOTO_RSSMS\LC4_Drawing\CA4_Drawing\CA4_Drawing\CA4_7062.dgn



AECOM

PROJECT
 TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE
 TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TUNNEL BUILDINGS, ELECTRICAL AND MECHANICAL WORKS

CLIENT
 路政署
HIGHWAYS DEPARTMENT
 港珠澳大橋管理處
 Hong Kong - Zhuhai - Macao Bridge
 Hong Kong Project Management Office

CONSULTANT
 AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS

Figure 1.2b

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK.
A	JAN.16	TENDER ADDENDUM NO.1	SYLC
	DEC.17	TENDER DRAWING	SYLC

STATUS

SCALE: A1 1:2500
 DIMENSION UNIT: MILLIMETRES

KEY PLAN

PROJECT NO.: 60240249
 CONTRACT NO.: HY/2017/10

SHEET TITLE
 ZONING PLAN (SHEET 2)

SHEET NUMBER
 60240249/C4/7062A

This drawing is the property of AECOM. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility and disclaims any liability whatsoever, in any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

Project Management Initials: Designer: KATH; Checked: SYLC; Approved: CWN ISO A1 554mm x 841mm

Plot File by: Jerrywong 17-Jan-18
 PATH: Y:\TO\To RSS\SL\C4 Drawings\C4 Drawings\C4 Drawings - DGN\60240249 C4_7063.dgn



PROJECT
 TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE
 TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TUNNEL BUILDINGS, ELECTRICAL AND MECHANICAL WORKS

CLIENT
 路政署
 HIGHWAYS DEPARTMENT
 港珠澳大橋香港工程管理有限公司
 Hong Kong - Zhuhai - Macao Bridge
 Hong Kong Project Management Office

CONSULTANT
 AECOM Asia Company Ltd.
 www.aecom.com

SUB-CONSULTANTS

Figure 1.2c

ISSUE/REVISION

NO.	DATE	DESCRIPTION	CHK.
A	JAN. 18	TENDER ADDENDUM NO. 1	SYLC
	DEC. 17	TENDER DRAWING	SYLC

STATUS

SCALE: A1 1:2500
 DIMENSION UNIT: MILLIMETRES

KEY PLAN

PROJECT NO. 60240249
 CONTRACT NO. HY/2017/10

SHEET TITLE
 ZONING PLAN (SHEET 3)

SHEET NUMBER
 60240249/C4/7063A

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or related upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. All measurements must be obtained from the stated dimensions.

1.2 SCOPE OF REPORT

This is the Thirteenth Monthly EM&A Report under the *Contract No. HY/2017/10 Tuen Mun – Chek Lap Kok Link – Northern Connection Tunnel Buildings, Electrical and Mechanical Works*. This report presents a summary of the environmental monitoring and audit works in June 2019.

1.3 ORGANIZATION STRUCTURE

The organization structure of the Contract is shown in *Appendix A*. The key personnel contact names and contact details are summarized in *Table 1.1* below.

Table 1.1 *Contact Information of Key Personnel*

Party	Position	Name	Telephone	Fax
HyD (Highways Department)	Project Coordinator	Joseph Lee	2762 4958	3188 6614
	Senior Engineer	Cheng Pan	2762 3383	3188 6614
ER (AECOM Asia Company Limited)	Principle Resident Engineer	S. W. Fok	2293 6200	2293 6300
	Resident Engineer	Desmond Fung	2293 6200	2293 6300
ENPO / IEC (Ramboll Hong Kong Ltd.)	ENPO Leader	Y.H. Hui	3465 2850	3465 2899
	IEC	Dr. F.C. Tsang	3465 2851	3465 2899
Contractor (Gammon Construction Limited)	Site Agent	Kenneth Tai	9039 4723	-
	Environmental Officer	Max Poon	9103 6303	-
ET (ERM-HK)	ET Leader	Dr. Jasmine Ng	2271 3311	2723 5660

1.4 SUMMARY OF CONSTRUCTION WORKS

The construction phase of the Contract commenced on 7 June 2018. The three-month rolling construction programme is shown in *Appendix B*.

As informed by the Contractor, details of the major works carried out in this reporting month are listed below:

Land-based Works


- Electrical and Mechanical Works and Architectural Builders Work and Finishes at Toll Control Building;
- Electrical and Mechanical Works at Ventilation Plant Room;
- Electrical and Mechanical Works at North Ventilation Building;

- Building Structure at Administration Building;
- Building Structure at Maintenance Depot;
- Building structure at Fire Services Department Building;
- Building Structure at Customs and Excise Department Building;
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Kiosk N2; and
- Electrical and Mechanical Works at the Tunnel;
- Electrical and Mechanical Works and Architectural Builders Work and Finishes at underpass at C3 area; and
- Building Structure at Satellite Control Building.

The locations of the construction activities are shown in *Figure 1.3*. The Environmental Sensitive Receivers in the vicinity of the Contract are shown in *Figure 1.4*.

The implementation schedule of environmental mitigation measures is presented in *Appendix C*.

Figure 1.3 *Locations of Major Construction Activities in the Reporting Month*

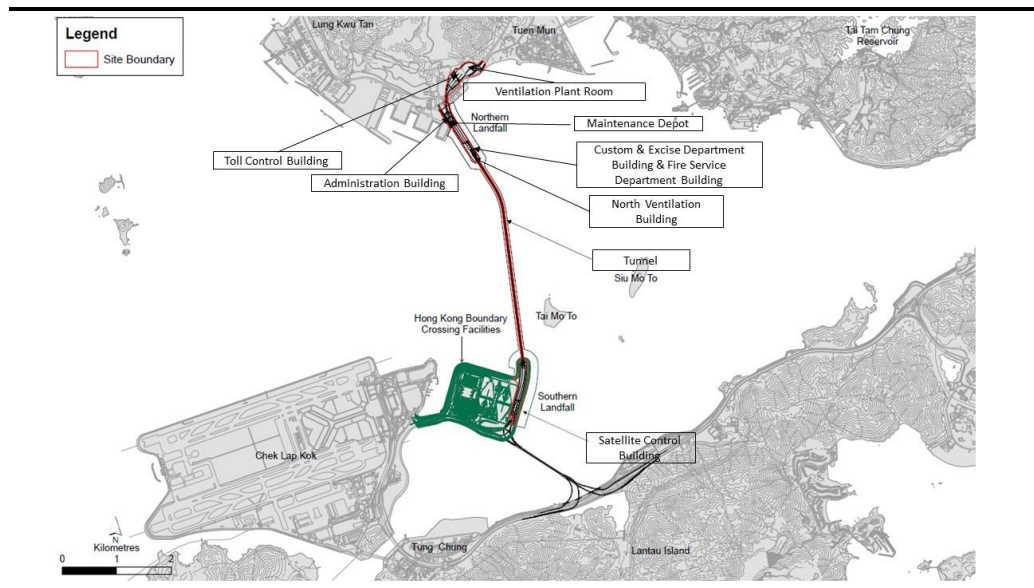

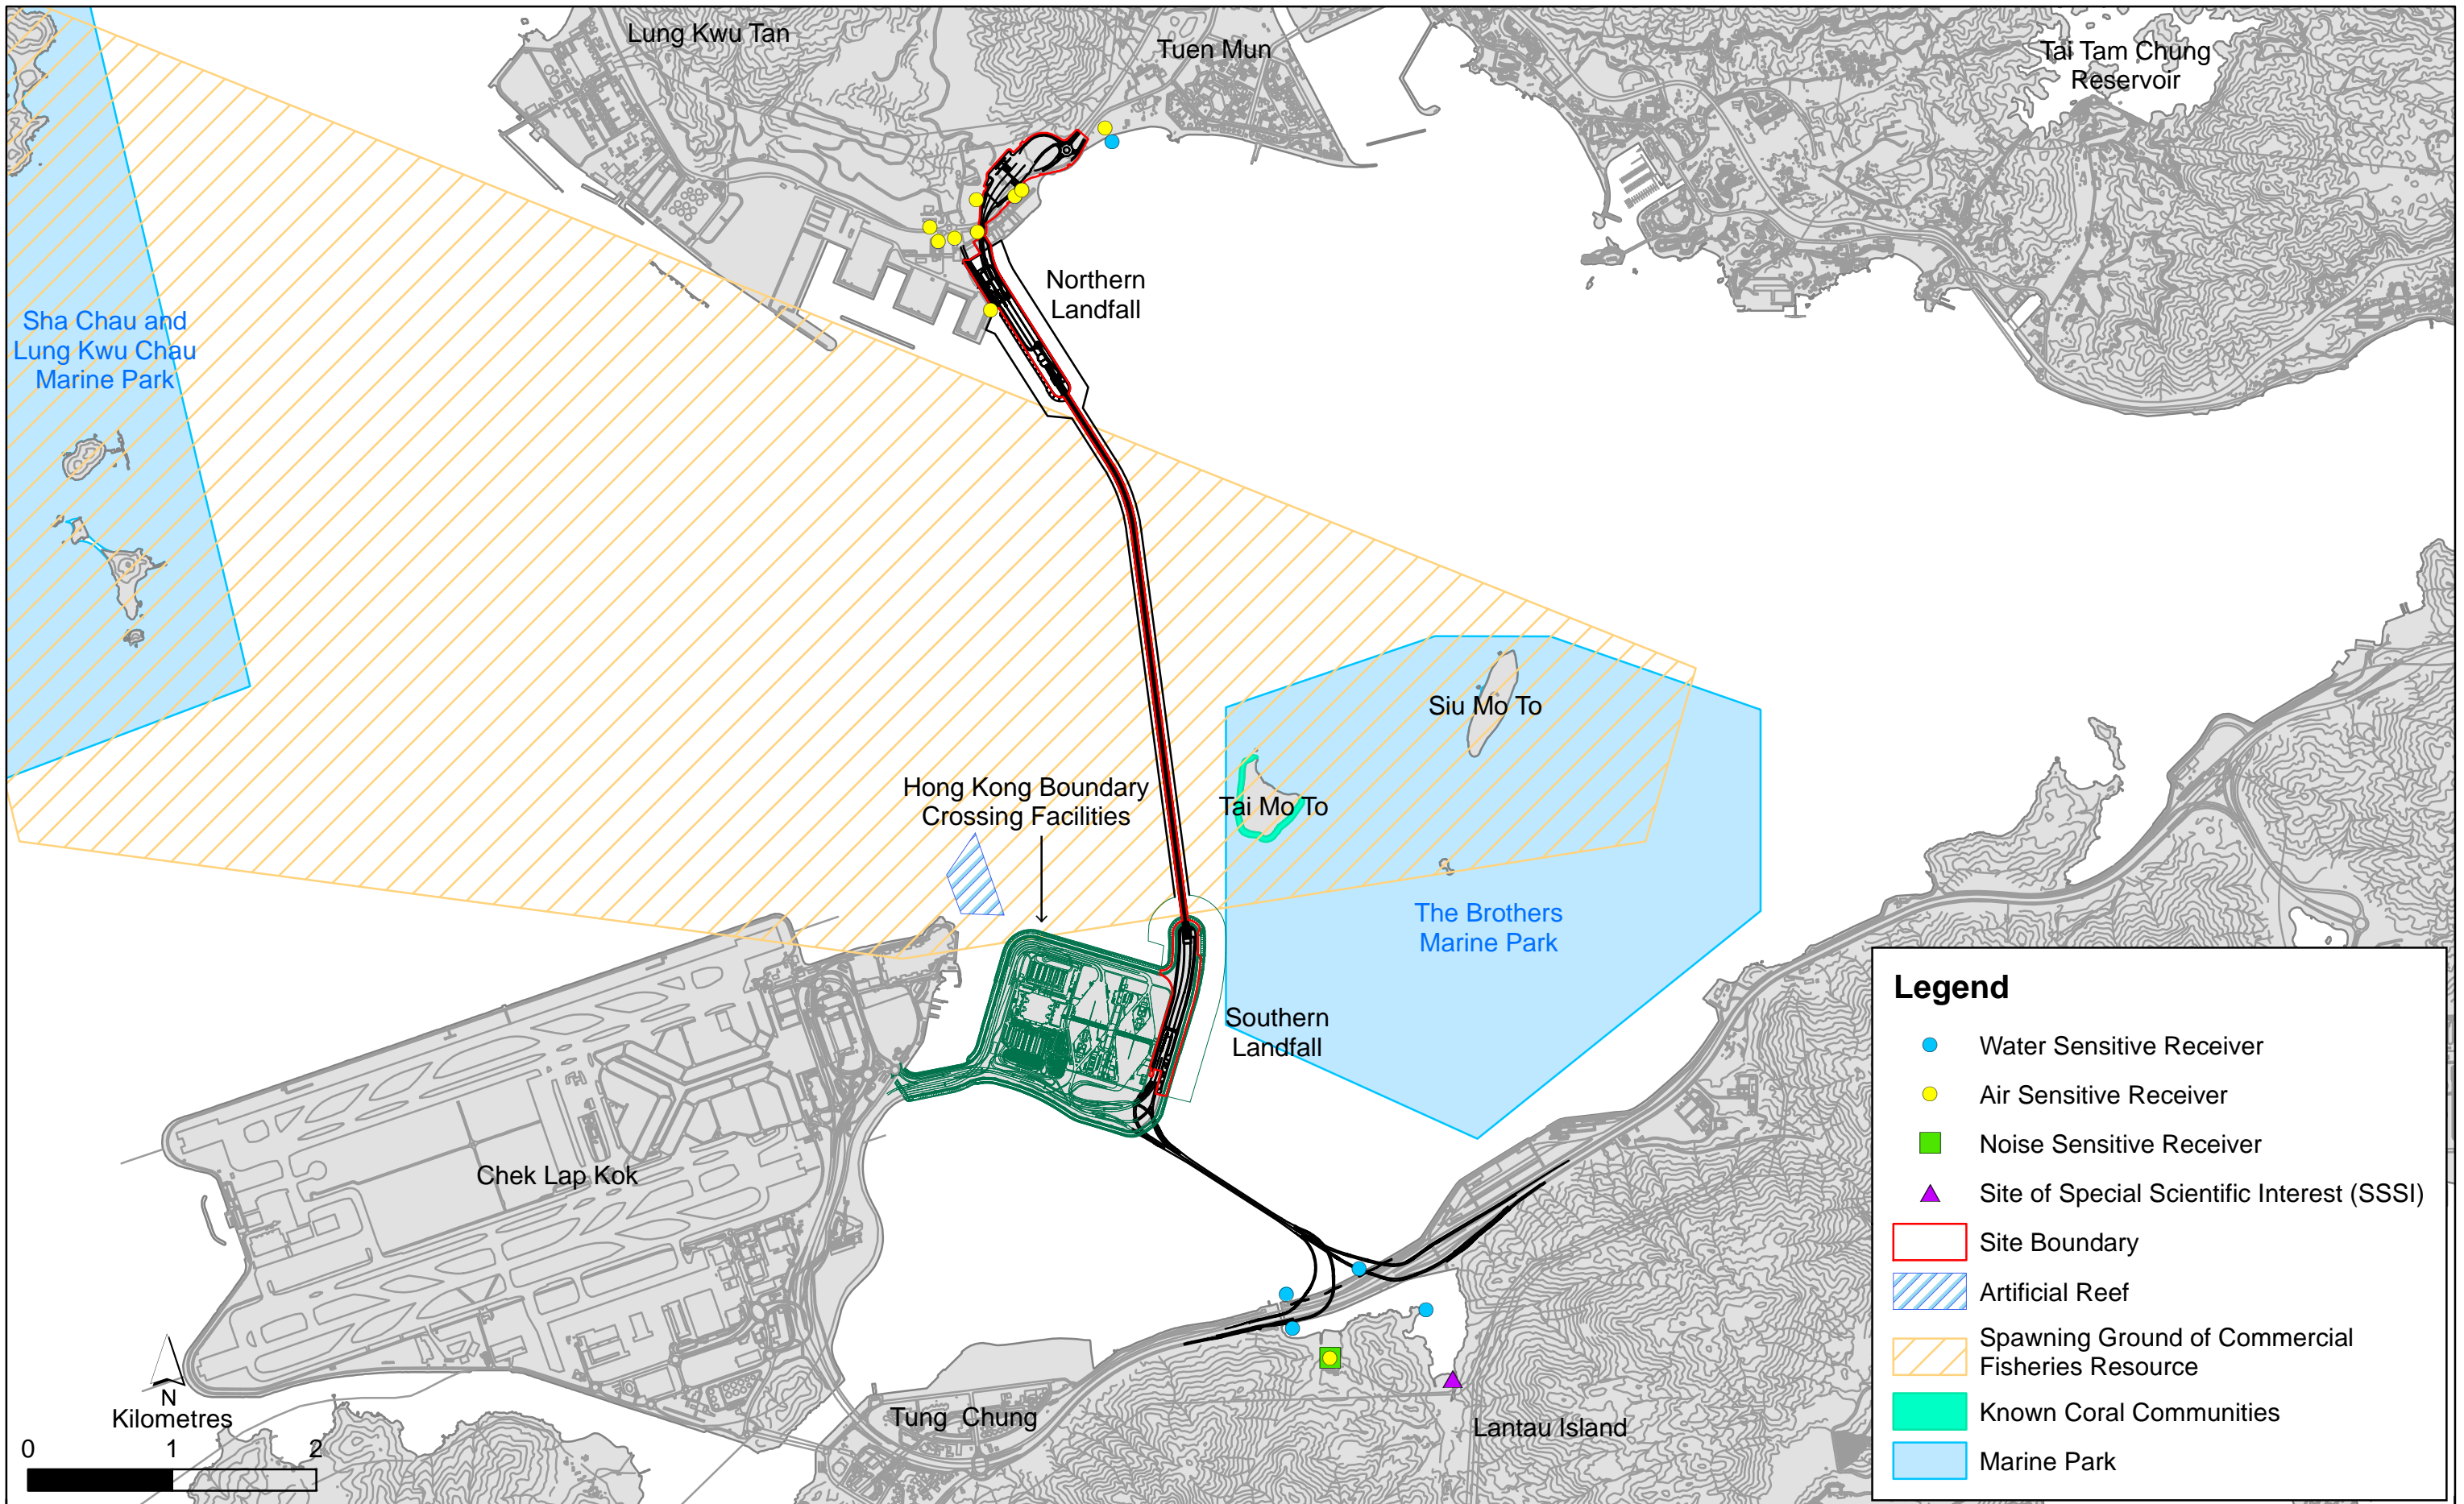


Figure 1.4

Environmental Sensitive Receivers in the Vicinity of the Project

The EM&A programme required environmental monitoring for air quality and environmental site inspections for air quality, water quality and waste management. The EM&A requirements and related findings for each component are summarized in the following sections

2.1 AIR QUALITY

2.1.1 Monitoring Requirements and Equipment

In accordance with the Updated EM&A Manual and the Enhanced TSP Monitoring Plan, impact 1-hour TSP monitoring was conducted three (3) times every six (6) days and impact 24-hour TSP monitoring was carried out once every six (6) days when the highest dust impact was expected. 1-hr and 24-hr TSP monitoring frequency was increased to three times per day every three days and daily every three days, respectively, as excavation works for launching shaft under *Contract No. HY/2012/08 Tuen Mun-Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section* commenced on 24 October 2014.

Results of air quality monitoring were adopted from the published EM&A data of *Contract No. HY/2012/08 Tuen Mun-Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section* ⁽¹⁾.

The Action and Limit Levels of the air quality monitoring were adopted from the published EM&A reports of *Contract No. HY/2012/08 Tuen Mun-Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section* ⁽²⁾. The Action and Limit Levels are provided in *Appendix D*.

The locations of the monitoring stations overlapped with Contract No. HY/2012/08 are shown in *Figure 2.1* and presented in *Table 2.1*.

Table 2.1 *Locations of Impact Air Quality Monitoring Stations and its Corresponding Monitoring Requirements*

Monitoring Station	Monitoring Dates	Location	Description	Parameters & Frequency
ASR1	1, 4, 7, 10, 13, 16, 19, 22, 25 and 28 June 2019	Tuen Mun Fireboat Station	Office	TSP monitoring
ASR5		Pillar Point Fire Station	Office	<ul style="list-style-type: none"> 1-hour Total Suspended Particulates (1-hour TSP, $\mu\text{g}/\text{m}^3$), 3 times in every 6 days 24-hour Total Suspended Particulates (24-hour TSP, $\mu\text{g}/\text{m}^3$), daily for 24-hour in every 6 days
AQMS1		Previous River Trade Golf	Bare ground	Enhanced TSP monitoring

(1) Published EM&A data for impact air quality monitoring by *Contract No. HY/2012/08* are available at: <http://www.hzmbenpo.com/>

(2) Published EM&A reports of *Contract No. HY/2012/08* are available at: <http://www.hzmbenpo.com/>

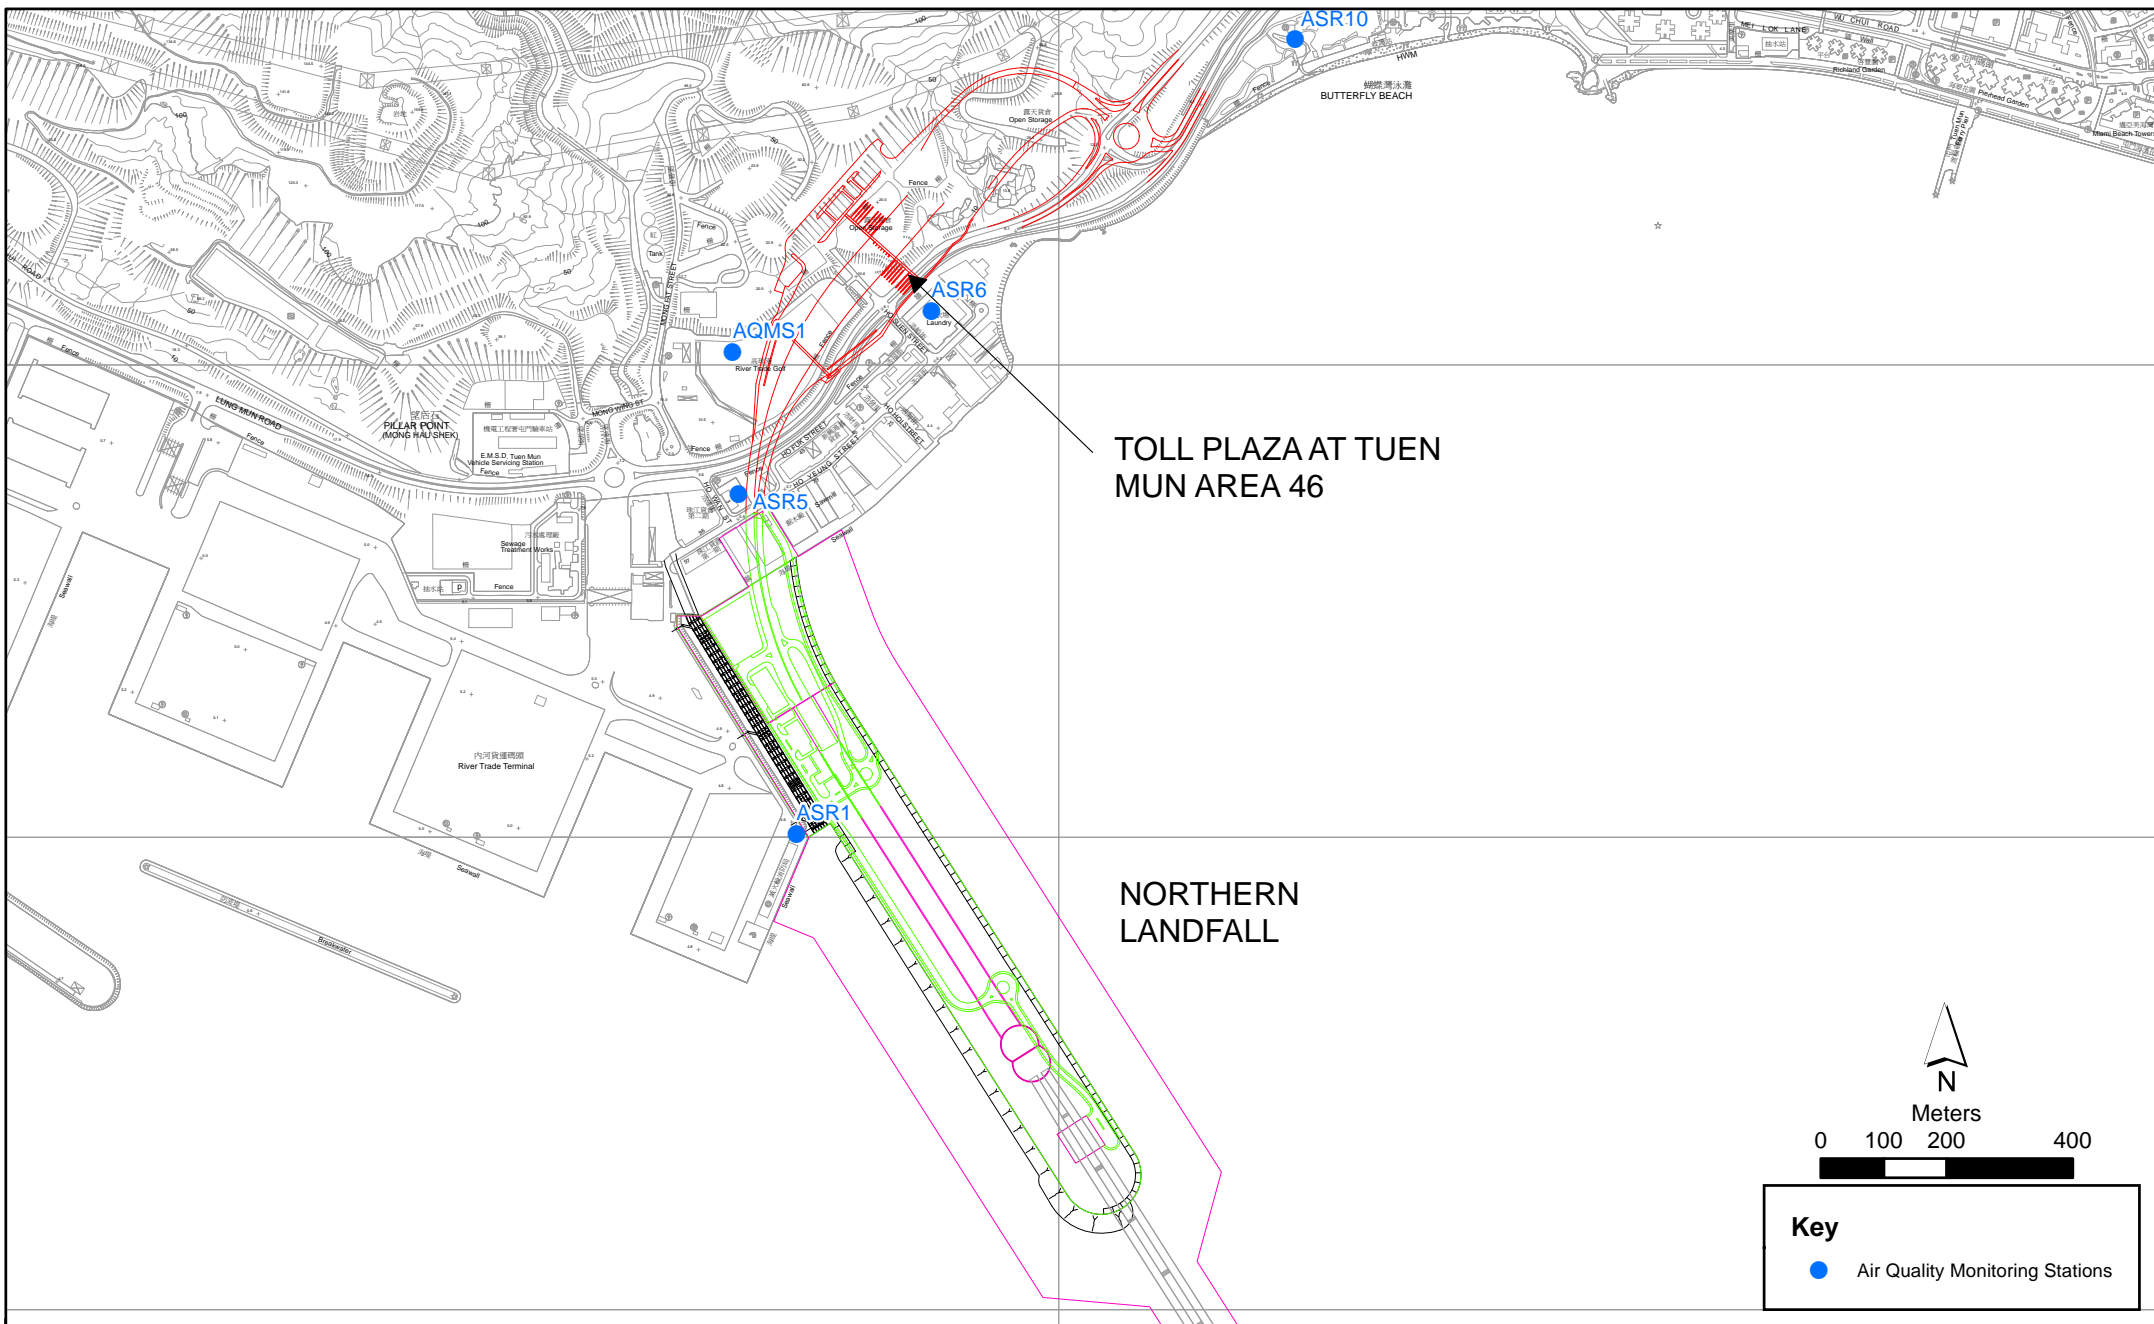


Figure 2.1

Air Quality Monitoring Stations for the Enhanced TSP Monitoring
 (Source: Adopted from Contract No. HY/2012/08 Tuen Mun-Chek Lap Kok Link -
 Northern Connection Sub-sea Tunnel Section)

Monitoring Station	Monitoring Dates	Location	Description	Parameters & Frequency
ASR6		Butterfly Beach Laundry	Office	(commenced on 24 October 2014 under <i>Contract No. HY/2012/08</i>)
ASR10		Butterfly Beach Park	Recreational uses	<ul style="list-style-type: none"> 1-hour Total Suspended Particulates (1-hour TSP, $\mu\text{g}/\text{m}^3$), 3 times in every 3 days 24-hour Total Suspended Particulates (24-hour TSP, $\mu\text{g}/\text{m}^3$), daily for 24-hour in every 3 days

2.1.2 *Results and Observations*

Results of air quality monitoring were adopted from the published EM&A data of *Contract No. HY/2012/08 Tuen Mun-Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section* ⁽¹⁾.

No exceedance of Action and Limit Levels of 1-hour TSP and 24-hour TSP was recorded by the Environmental Team of *Contract No. HY/2012/08* during the reporting period. No action is required to be undertaken in accordance with the Event Action Plan as presented in *Appendix E*.

2.2 *LANDFILL GAS HAZARD MONITORING*

No excavation work was conducted at the excavation area in June 2019 and thus landfill gas hazard monitoring was temporarily suspended in June 2019.

2.3 *EM&A SITE INSPECTION*

Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. In the reporting month, four (4) site inspections were carried out on 6, 14, 21 and 28 June 2019.

Key observations and recommendations during the site inspections in this reporting period are summarized in *Table 2.3*.

Table 2.3 *Specific Observations and Recommendations during the Weekly Site Inspection in this Reporting Month*

Inspection Date	Observations	Recommendations/Remarks
6 June 2019	Toll Control Building <ul style="list-style-type: none"> The chemical container on the ground should be removed. Toll booth <ul style="list-style-type: none"> Water spraying should be applied during dusty conditions. 	Toll Control Building <ul style="list-style-type: none"> The Contractor was reminded to remove the chemical container on the ground. Toll booth <ul style="list-style-type: none"> The Contractor was reminded to apply water spraying during dusty conditions.

(1) Published EM&A data for impact air quality monitoring by *Contract No. HY/2012/08* are available at: <http://www.hzmbenpo.com/>

Inspection Date	Observations	Recommendations/ Remarks
14 June 2019	North Ventilation Building <ul style="list-style-type: none"> • Consturction waste should be sorted. • Accumulated waste in the refuse skip should be removed. 	North Ventilation Building <ul style="list-style-type: none"> • The Contractor was reminded to sort construction waste. • The Contractor was reminded to remove accumulated waste in the refuse skip.
21 June 2019	Maintenance Depot <ul style="list-style-type: none"> • Chemical container was observed without drip tray. • Concrete bags should be covered with tarpaulin. Administration Building <ul style="list-style-type: none"> • Waste should be sorted for disposal. 	Maintenance Depot <ul style="list-style-type: none"> • The Contractor was reminded to place chemical container in drip tray. • The Contractor was reminded to cover concrete bags with tarpaulin. Administration Building <ul style="list-style-type: none"> • The Contractor was reminded to sort waste for disposal.
28 June 2019	North Ventilation Building <ul style="list-style-type: none"> • Accumulated waste should be removed. Customs and Excise Building <ul style="list-style-type: none"> • Waste should be sorted properly for disposal. 	North Ventilation Building <ul style="list-style-type: none"> • The Contractor was reminded to remove accumulated waste. Customs and Excise Building <ul style="list-style-type: none"> • The Contractor was reminded to sort waste properly for disposal.

The Contractor has rectified all of the observations as identified during environmental site inspections in the reporting month.

2.4 WASTE MANAGEMENT STATUS

The Contractor had submitted application form for registration as chemical waste producer under the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.

Wastes generated during this reporting period included mainly construction wastes (inert and non-inert). Reference has been made to the waste flow table prepared by the Contractor (*Appendix F*). The quantities of different types of wastes are summarized in *Table 2.4*.

Table 2.4 Quantities of Different Waste Generated in the Reporting Month

Month/Year	Inert C&D Materials ^(a) (m ³)	Inert Construction Waste Re-used (m ³)	Non-inert Construction Waste ^(b) (kg)	Imported Fill (m ³)	Recyclable Materials ^(c) (kg)	Chemical Wastes (kg)
June 2019	11	8	118,070	0	0	0

Notes:

- (a) Inert construction wastes include hard rock and large broken concrete disposed as public fill.
- (b) Non-inert construction wastes include general refuse disposed at landfill.
- (c) Recyclable materials include metals, paper, cardboard, plastics, timber and others.

The Contractor was advised to properly maintain on site C&D materials and waste collection, sorting and recording system, dispose of C&D materials and wastes at designated ground and maximize reuse/ recycle of C&D materials and wastes. The Contractor was also reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly.

For chemical waste containers, the Contractor was reminded to treat properly and store temporarily in designated chemical waste storage area on site in accordance with the *Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes*.

2.5 *ENVIRONMENTAL LICENSES AND PERMITS*

The status of environmental licensing and permit is summarized in *Table 2.5* below.

Table 2.5 Summary of Environmental Licensing and Permit Status

License/ Permit	License or Permit No.	Date of Issue	Date of Expiry	License/ Permit Holder	Remarks
Environmental Permit	EP-354/2009/D	13 March 2015	N/A	HyD	Tuen Mun- Chek Lap Kok Link
APCO Construction Dust Notification	433493	14 May 2018	N/A	GCL	For Tuen Mun working area
Construction Waste Billing Account	7030836	15 May 2018	N/A	GCL	N/A
Chemical Waste Producer Registration	5213-422-G2827-01	13 June 2018	N/A	GCL	N/A
Discharge License under WPCO for Buildings at C2 area	WT00031783-2018	22 October 2018	31 October 2023	GCL	Sampling Frequency: Bimonthly
Discharge License under WPCO for Buildings at C3 area	WT00032062-2018	30 October 2018	31 October 2023	GCL	Sampling Frequency: Quarterly
Construction Noise Permit	GW-RW0267-19	21 June 2019	14 October 2019	GCL	For Toll Control Building, Administration Building, Maintenance Depot, FSD, C&ED, Boundary Wall, Tunnel, Approach ramp, NVB and WA18
Construction Noise Permit	GW-RS0340-19	18 April 2019	17 October 2019	GCL	For Kiosk S2 and SCB

2.6 *IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES*

In response to the site audit findings, the Contractors carried out all corrective actions.

A summary of the Implementation Schedule of Environmental Mitigation Measures (EMIS) is presented in *Appendix C*. The necessary mitigation measures relevant to this Contract were implemented properly.

The landscape and visual (L&V) mitigation measures were also monitored on weekly basis in the reporting period. The monitoring status is summarized in *Appendix C*.

2.7 *SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMANCE LIMIT*

No exceedance of Action and Limit Levels of 1-hour TSP and 24-hour TSP was recorded by the Environmental Team of Contract No. *HY/2012/08* during the reporting period. No action is required to be undertaken in accordance with the Event Action Plan as presented in *Appendix E*.

No excavation work was conducted at the excavation area in June 2019 and thus landfill gas hazard monitoring was temporarily suspended in June 2019.

Cumulative statistics are provided in *Appendix G*.

2.8 *SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS*

The Environmental Complaint Handling Procedure is provided in *Figure 2.2*.

There was no environmental complaint, notification of summons or successful prosecution recorded in the reporting period.

Statistics on complaints, notifications of summons, successful prosecutions are summarized in *Appendix G*.

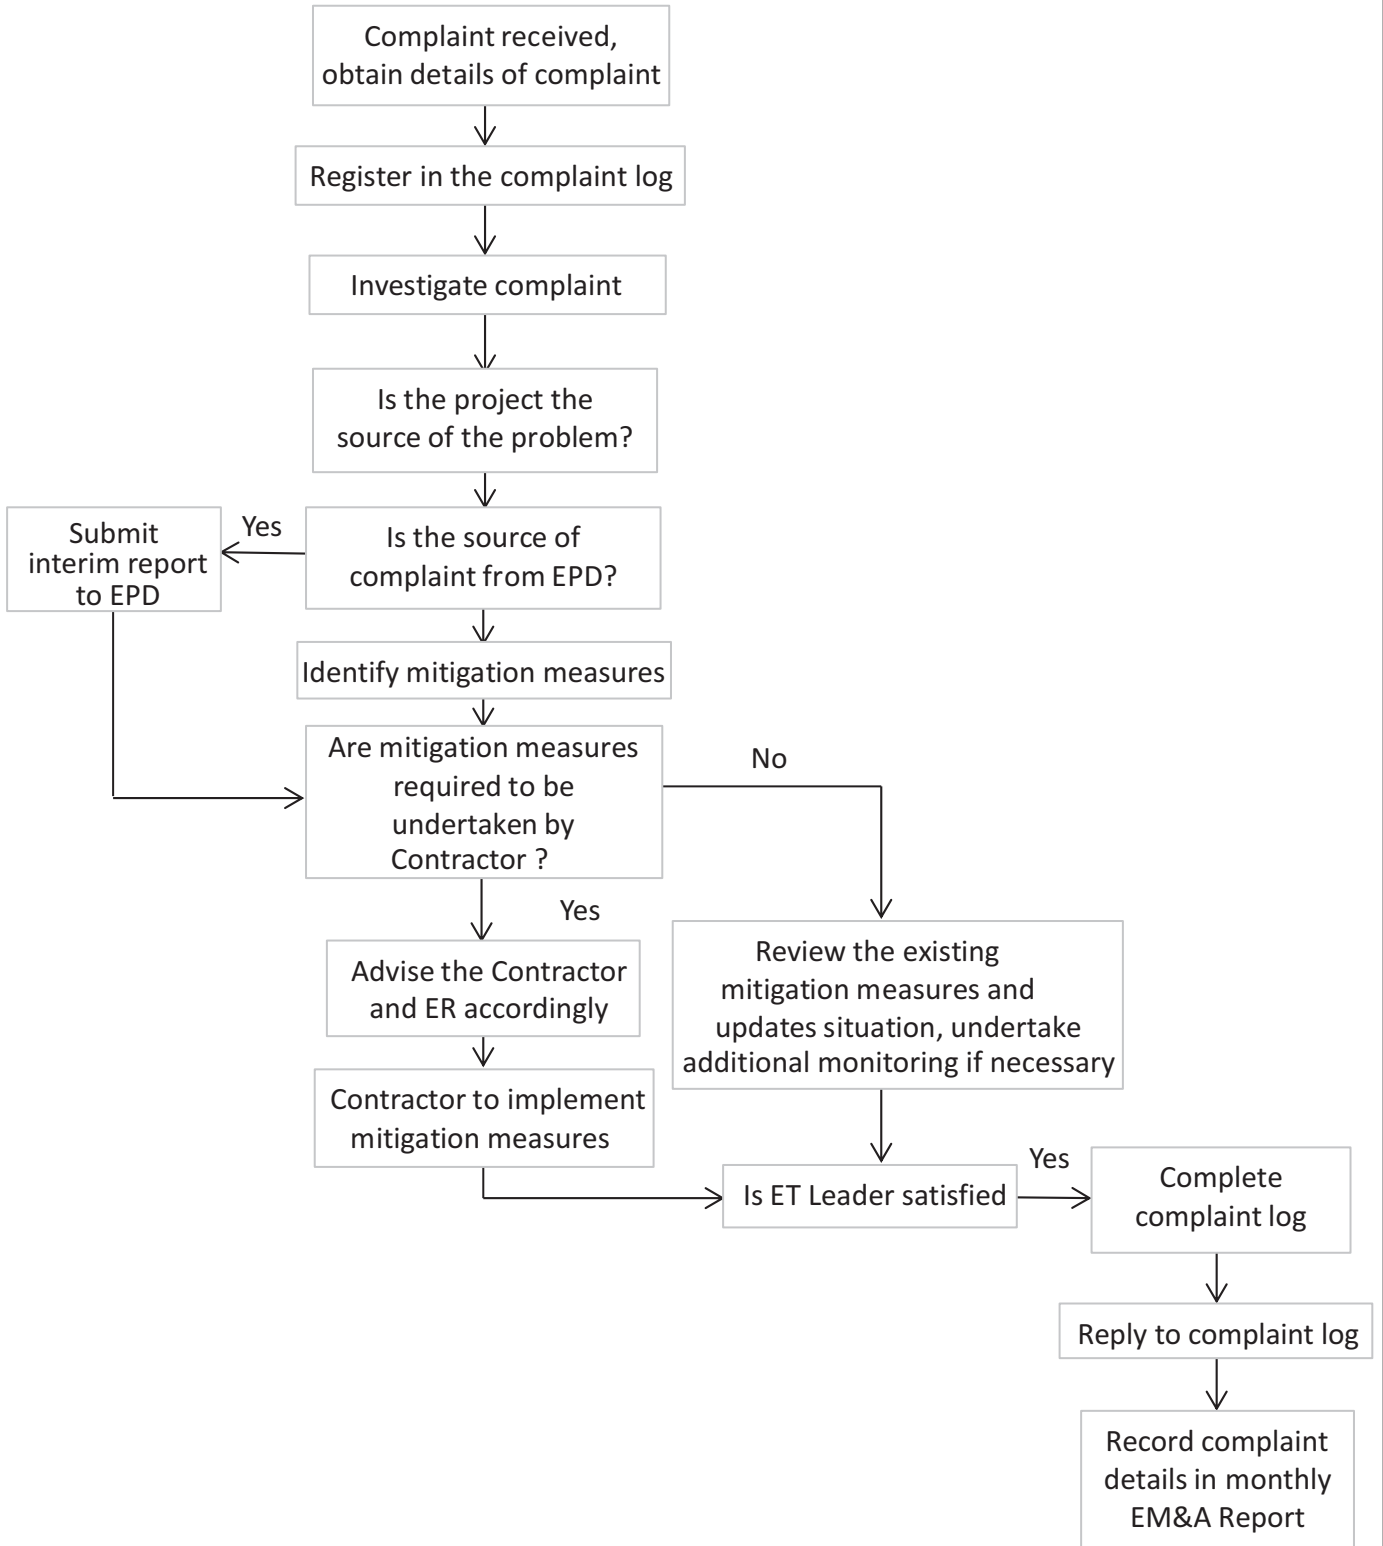


Figure 2.2

Environmental Complaint Handling Procedure

3.1 CONSTRUCTION ACTIVITIES FOR THE COMING MONTH

As informed by the Contractor, the major works for the Contract in July 2019 will be:

Land-based Works

- Electrical and Mechanical Works and Architectural Builders Work and Finishes at Toll Control Building;
- Electrical and Mechanical Works at Ventilation Plant Room;
- Electrical and Mechanical Works at North Ventilation Building;
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Administration Building;
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Maintenance Depot;
- Building structure at Fire Services Department Building;
- Building Structure at Customs and Excise Department Building;
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Kiosk N2; and
- Electrical and Mechanical Works and Architectural Builder's Work and Finishes at the Tunnel;
- Electrical and Mechanical Works and Architectural Builders Work and Finishes at underpass at C3 area; and
- Building Structure at Satellite Control Building.

3.2 KEY ISSUES FOR THE COMING MONTH

Potential environmental impacts arising from the above upcoming construction activities in the next reporting month of July 2019 are mainly associated with dust and waste management issues.

4.1 CONCLUSIONS

This Thirteenth Monthly EM&A Report presents the findings of the EM&A activities undertaken during the period from 1 to 30 June 2019, in accordance with the Updated EM&A Manual and the requirements of EP-354/2009/D.

Air quality (including 1-hour TSP and 24-hour TSP) monitoring were carried out in this reporting month.

No exceedance of Action and Limit Levels of 1-hour TSP and 24-hour TSP was recorded by the Environmental Team of Contract No. *HY/2012/08* during the reporting period. No action is required to be undertaken in accordance with the Event Action Plan as presented in *Appendix E*.

No excavation work was conducted at the excavation area in June 2019 and thus landfill gas hazard monitoring was temporarily suspended in June 2019.


Environmental site inspection was carried out four (4) times in June 2019. Remedial actions recommended for the deficiencies identified during the site audits were properly implemented by the Contractor.

There was no environmental complaint, notification of summons or successful prosecution recorded in the reporting period.

The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Appendix A

Project Organization for Environmental Works

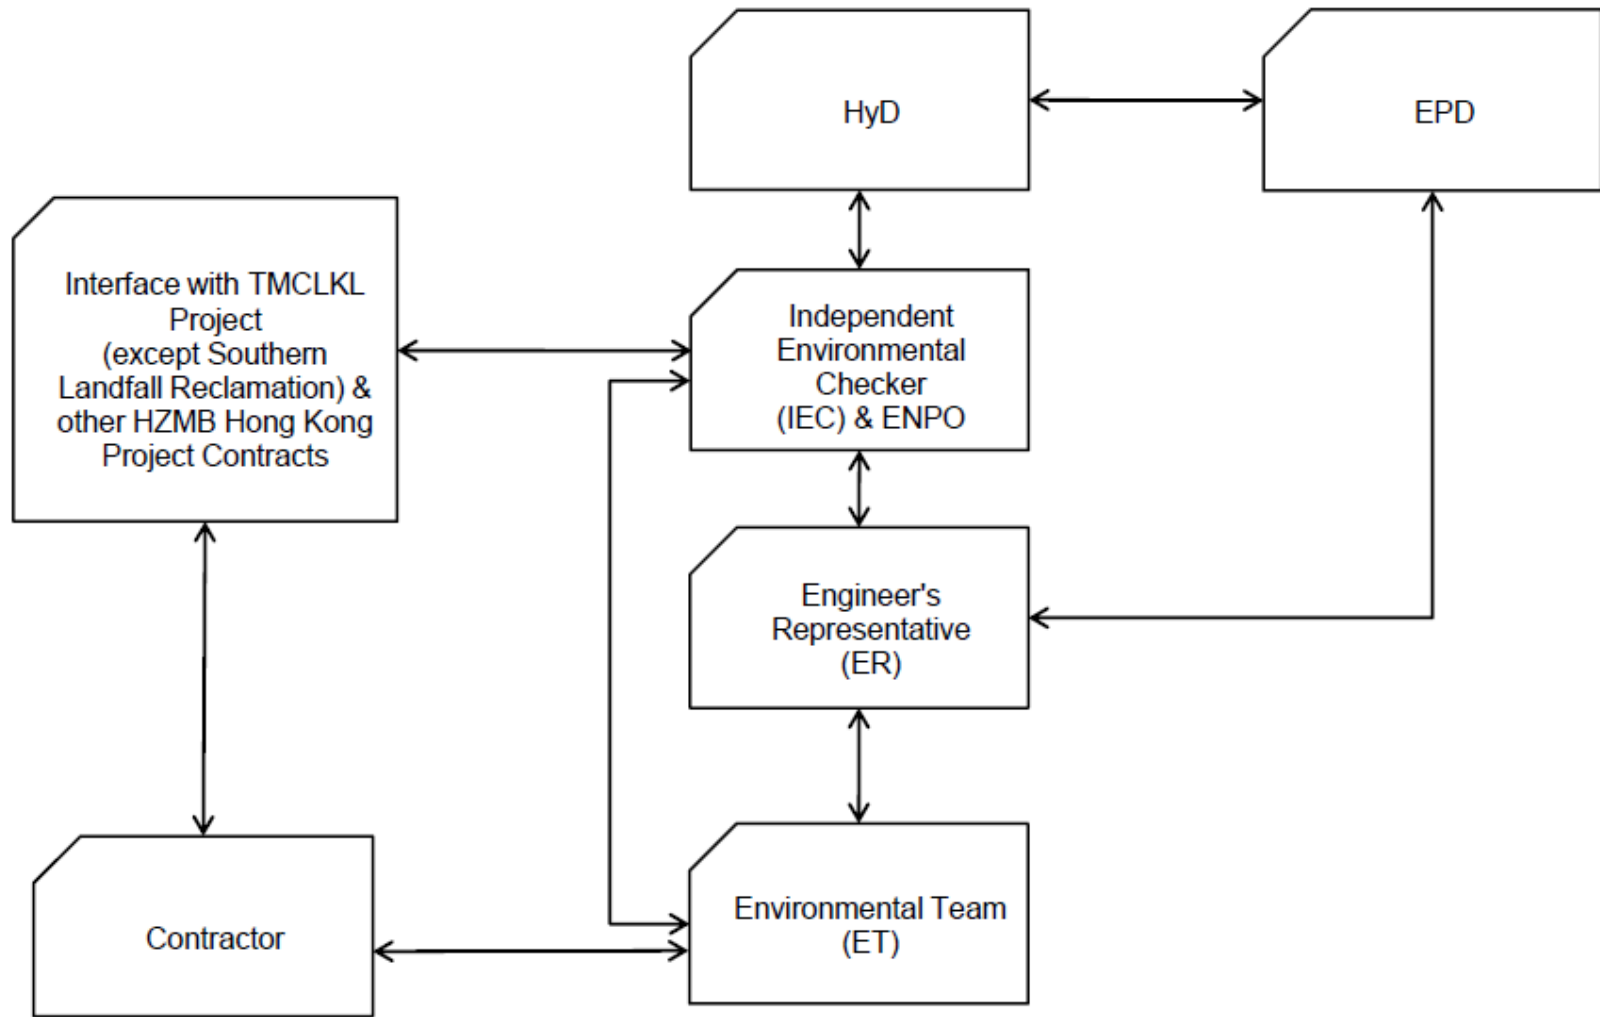

↔ Line of Communication

Appendix B

Construction Programme

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
HY2017/10 - Works Programme Three Month Rolling Programme of 20-Jun-19											
Contract Dates											
Key Dates											
KD01	KD01 - Toll Control Bldg & TCSS Provision	0	100%	0	31-May-19		◆				
KD02	KD02 - Admin Bldg, Maintenance Depot, Kiosk N2, & TCSS Provision	0	0%	0	28-Aug-19*					◆	
KD04	KD04 - Underpass/Roundabout Area & TCSS Provision	0	0%	0	30-Jul-19*			◆			
Portion Access Dates											
P2010	Access to Portion VII SVB Basement BL1	0	0%	0	30-Jun-19			◆			
P2020	Access to Portion VII SVB G/F	0	0%	0	31-Jul-19				◆		
P2030	Access to Portion VII SVB 1/F	0	0%	0	30-Aug-19					◆	
P320	Access to Portion III (Day 437)	0	0%	0	17-Jul-19			◆			
Portion Possession Dates											
P270	Possession to Portion XIX (Day 390)	0	0%	0	20-Jun-19		◆				
P285	Possession to Portion XI (Day 390)	0	0%	0	20-Jun-19		◆				
P290	Possession to Portion XXIIa (Day 390)	0	0%	0	20-Jun-19		◆				
P295	Possession to Portion IX (Day 390)	0	0%	0	20-Jun-19		◆				
P300	Possession to Portion XXIIb (Day 390)	0	0%	0	20-Jun-19		◆				
P305	Possession to Portion X (Day 390)	0	0%	0	20-Jun-19		◆				
P315	Possession to Portion XXIIc (Day 390)	0	0%	0	20-Jun-19		◆				
P325	Possession to Portion XXII (Day 483)	0	0%	0	01-Sep-19					◆	
P335	Possession to Portion XXIII (Day 483)	0	0%	0	01-Sep-19					◆	
P345	Possession to Portion VIb (Day 483)	0	0%	0	01-Sep-19					◆	
Major Design Submission & Approval											
Toll Control Building											
MVAC System											
TCB-EMD1095	Authorities Review and Comment of AHU/PAU Static Pressure Calculation	56	50%	28	23-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
TCB-EMD1115	Authorities Review and Comment of MVAC Pump head calculation	56	50%	28	23-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
Electrical System											
TCB-EMD1015	Authorities Review and Comment of UPS and Battery Capacity Calculations	56	50%	28	22-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
TCB-EMD1055	Authorities Review and Comment of Generator Calculation	56	50%	28	15-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
TCB-EMD1305	Submission of System Design of PV System	0	100%	0	28-May-19 A		◆				
TCB-EMD1315	ER Review and Comment of System Design of PV System	26	100%	0	28-May-19 A	10-Jun-19 A	[Gantt bar: blue from Jun 20 to Jun 28]				
TCB-EMD1325	Preparation and Resubmission of System Design of PV System	26	50%	13	11-Jun-19 A	05-Jul-19	[Gantt bar: blue from Jun 20 to Jul 05, red from Jun 28 to Jul 05]				
TCB-EMD1335	ER Review and Approval of System Design of PV System	13	0%	13	06-Jul-19	20-Jul-19	[Gantt bar: red from Jul 06 to Jul 20]				
TCB-EMD1345	Authorities Review and Comment of PV System	56	50%	28	28-May-19 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
Fire Service System											
TCB-EMD1175	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	01-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
TCB-EMD1195	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	14-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
TCB-EMD1215	Authorities Review and Comment of FM200 System Design Calculation	56	50%	28	13-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
Plumbing & Drainage System											
TCB-EMD1235	Authorities Review and Comment of Pump Head Calculation	56	50%	28	07-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
TCB-EMD1275	Authorities Review and Comment of Hot water system capacity calculation	56	50%	28	07-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
TCB-EMD1395	Authorities Review and Comment of Drainage Sump Pumps and Pump Pits Calculation	56	50%	28	23-Jul-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
Administration Building											
MVAC System											
ADB-EMD1015	Authorities Review and Comment of AC Cooling Capacity Calculation	56	50%	28	17-Aug-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
ADB-EMD1035	Authorities Review and Comment of AHU/PAU Static Pressure Calculation	56	50%	28	08-Oct-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				
ADB-EMD1055	Authorities Review and Comment of Pump head calculation	56	50%	28	07-Nov-18 A	23-Jul-19	[Gantt bar: blue from Jun 20 to Jul 23, green from Jul 23 to Jul 23]				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 1/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
ADB-EMD1075	Authorities Review and Comment of Mechanical Ventilation Capacity Calculation	56	50%	28	17-Aug-18 A	23-Jul-19				
Electrical System										
ADB-EMD1115	Authorities Review and Comment of Electrical Loading Demand Calculation	56	50%	28	27-Aug-18 A	23-Jul-19				
ADB-EMD1135	Authorities Review and Comment of Generator Calculation	56	50%	28	09-Aug-18 A	23-Jul-19				
ADB-EMD1305	Submission of System Design of PV System	0	100%	0	28-May-19 A					
ADB-EMD1315	ER Review and Comment of System Design of PV System	26	100%	0	28-May-19 A	10-Jun-19 A				
ADB-EMD1325	Preparation and Resubmission of System Design of PV System	26	50%	13	11-Jun-19 A	05-Jul-19				
ADB-EMD1335	ER Review and Approval of System Design of PV System	13	0%	13	06-Jul-19	20-Jul-19				
ADB-EMD1345	Authorities Review and Comment of System Design of PV System	56	50%	28	28-May-19 A	23-Jul-19				
Fire Service System										
ADB-EMD1155	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	13-Aug-18 A	23-Jul-19				
ADB-EMD1175	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	13-Aug-18 A	23-Jul-19				
ADB-EMD1195	Authorities Review and Comment of FM200 System Design Calculation	56	50%	28	13-Aug-18 A	23-Jul-19				
Plumbing & Drainage System										
ADB-EMD1215	Authorities Review and Comment of Pump Head Calculation	56	50%	28	25-Aug-18 A	23-Jul-19				
ADB-EMD1235	Authorities Review and Comment of Pressure Vessel Calculation	56	50%	28	25-Aug-18 A	23-Jul-19				
ADB-EMD1255	Authorities Review and Comment of Hot water system capacity calculation	56	50%	28	25-Aug-18 A	23-Jul-19				
North Ventilation Building										
MVAC System										
NVB-EMD1035	Authorities Review and Comment of Mechanical Ventilation Capacity Calculation	56	50%	28	26-Sep-18 A	23-Jul-19				
Electrical System										
NVB-EMD1055	Authorities Review and Comment of HV Electrical Loading Calculation	56	50%	28	26-Sep-18 A	23-Jul-19				
NVB-EMD1075	Authorities Review and Comment of UPS and Battery Capacity Calculations	56	50%	28	17-Aug-18 A	23-Jul-19				
NVB-EMD1095	Authorities Review and Comment of Electrical Loading Demand Calculation	56	50%	28	03-Sep-18 A	23-Jul-19				
NVB-EMD1115	Authorities Review and Comment of Generator Calculation	56	50%	28	17-Aug-18 A	23-Jul-19				
Fire Service System										
NVB-EMD1135	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	01-Aug-18 A	23-Jul-19				
NVB-EMD1155	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	14-Aug-18 A	23-Jul-19				
NVB-EMD1175	Authorities Review and Comment of FM200 System Design Calculation	28	50%	14	13-Aug-18 A	06-Jul-19				
Plumbing & Drainage System										
NVB-EMD1305	Authorities Review and Comment of Drainage Sump Pumps and Pump Pits Calculation	56	50%	28	07-Aug-18 A	23-Jul-19				
Maintenance Depot										
MVAC System										
MD-EMD1015	Authorities Review and Comment of AC Cooling Capacity Calculation	56	50%	28	17-Aug-18 A	23-Jul-19				
Electrical System										
MD-EMD1075	Authorities Review and Comment of Electrical Loading Demand Calculation	56	50%	28	27-Aug-18 A	23-Jul-19				
MD-EMD1095	Authorities Review and Comment of Generator Calculation	56	50%	28	06-Oct-18 A	23-Jul-19				
Fire Service System										
MD-EMD1115	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	14-Aug-18 A	23-Jul-19				
MD-EMD1135	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	14-Aug-18 A	23-Jul-19				
MD-EMD1155	Authorities Review and Comment of FM200 System Design Calculation	56	50%	28	14-Aug-18 A	23-Jul-19				
Plumbing & Drainage System										
MD-EMD1175	Authorities Review and Comment of Pump Head Calculation	56	50%	28	13-Aug-18 A	23-Jul-19				
MD-EMD1195	Authorities Review and Comment of Pressure Vessel Calculation	56	50%	28	13-Aug-18 A	23-Jul-19				
MD-EMD1215	Authorities Review and Comment of Drainage Sump Pumps and Pump Pits Calculation	56	50%	28	27-Aug-18 A	23-Jul-19				
Satellite Control Building										
MVAC System										
SCB-EMD1015	Authorities Review and Comment of AC Cooling Capacity Calculation	56	50%	28	17-Aug-18 A	23-Jul-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 2/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
Electrical System										
SCB-EMD1055	Authorities Review and Comment of UPS and Battery Capacity Calculations	56	50%	28	05-Sep-18 A	23-Jul-19				
SCB-EMD1075	Authorities Review and Comment of Electrical Loading Demand Calculation	56	50%	28	01-Nov-18 A	23-Jul-19				
SCB-EMD1095	Authorities Review and Comment of Generator Calculation	56	50%	28	27-Nov-18 A	23-Jul-19				
Fire Service System										
SCB-EMD1115	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	14-Aug-18 A	23-Jul-19				
SCB-EMD1135	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	14-Aug-18 A	23-Jul-19				
SCB-EMD1155	Authorities Review and Comment of FM200 System Design Calculation	56	50%	28	14-Aug-18 A	23-Jul-19				
Plumbing & Drainage System										
SCB-EMD1285	Authorities Review and Comment of Pump Head Calculation	56	50%	28	27-Aug-18 A	23-Jul-19				
SCB-EMD1335	Authorities Review and Comment of Pressure Vessel Calculation	56	50%	28	27-Aug-18 A	23-Jul-19				
Costom & Excise Department Building										
Electrical System										
CEDB-EMD1015	Authorities Review and Comment of UPS and Battery Capacity Calculations	56	50%	28	01-Nov-18 A	23-Jul-19				
CEDB-EMD1035	Authorities Review and Comment of Electrical Loading Demand Calculation	56	50%	28	01-Nov-18 A	23-Jul-19				
CEDB-EMD1055	Authorities Review and Comment of Generator Calculation	56	50%	28	27-Nov-18 A	23-Jul-19				
Fire Service System										
CEDB-EMD1075	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	21-Dec-18 A	23-Jul-19				
CEDB-EMD1095	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	08-Oct-18 A	23-Jul-19				
Plumbing & Drainage System										
CEDB-EMD1135	Authorities Review and Comment of Pump Head Calculation	56	50%	28	07-Sep-18 A	23-Jul-19				
CEDB-EMD1155	Authorities Review and Comment of Pressure Vessel Calculation	56	50%	28	05-Sep-18 A	23-Jul-19				
Fire Services Department Building										
Electrical System										
FSDB-EMD1015	Authorities Review and Comment of UPS and Battery Capacity Calculations	56	50%	28	01-Nov-18 A	23-Jul-19				
FSDB-EMD1035	Authorities Review and Comment of Electrical Loading Demand Calculation	56	50%	28	01-Nov-18 A	23-Jul-19				
FSDB-EMD1055	Authorities Review and Comment of Generator Calculation	56	50%	28	27-Nov-18 A	23-Jul-19				
Fire Service System										
FSDB-EMD1075	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	07-Sep-18 A	23-Jul-19				
FSDB-EMD1095	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	07-Sep-18 A	23-Jul-19				
FSDB-EMD1205	Authorities Review and Comment of FM200 System Design Calculation	56	50%	28	07-Sep-18 A	23-Jul-19				
Plumbing & Drainage System										
FSDB-EMD1135	Authorities Review and Comment of Pump Head Calculation	56	50%	28	05-Sep-18 A	23-Jul-19				
FSDB-EMD1155	Authorities Review and Comment of Pressure Vessel Calculation	56	50%	28	05-Sep-18 A	23-Jul-19				
South Ventilation Building										
MVAC System										
SVB-EMD1015	Authorities Review and Comment of Staircase Pressurization System Calculation	56	50%	28	24-Jan-19 A	23-Jul-19				
SVB-EMD1035	Authorities Review and Comment of Mechanical Ventilation Capacity Calculation	56	50%	28	11-Sep-18 A	23-Jul-19				
Electrical System										
SVB-EMD1055	Authorities Review and Comment of HV Electrical Loading Calculation	56	50%	28	01-Nov-18 A	23-Jul-19				
SVB-EMD1095	Authorities Review and Comment of Electrical Loading Demand Calculation	56	50%	28	28-Nov-18 A	23-Jul-19				
SVB-EMD1115	Authorities Review and Comment of Generator Calculation	56	50%	28	07-Dec-18 A	23-Jul-19				
Fire Service System										
SVB-EMD1135	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	21-Dec-18 A	23-Jul-19				
SVB-EMD1155	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	21-Dec-18 A	23-Jul-19				
SVB-EMD1175	Authorities Review and Comment of FM200 System Design Calculation	56	50%	28	30-Nov-18 A	23-Jul-19				
Vehicular Underpass										
Fire Service System										

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 3/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
VU-EMD1025	Authorities Review and Comment of Foam system design calculation	56	50%	28	09-Aug-18 A	23-Jul-19				
Plumbing & Drainage System										
VU-EMD1045	Authorities Review and Comment of Pump Head Calculation	56	50%	28	27-Sep-18 A	23-Jul-19				
Tunnel Lighting System										
VU-EMD1145	Authorities Review and Comment of Design Proposal of Tunnel Lighting System (TLS)	56	50%	28	29-Aug-18 A	23-Jul-19				
VU-EMD1165	Authorities Review and Comment of Tunnel Lighting Lux Calculation	56	50%	28	31-Dec-18 A	23-Jul-19				
Tunnel										
Fire Service System										
TUN-EMD1035	Authorities Review and Comment of Foam system design calculation	56	50%	28	09-Aug-18 A	23-Jul-19				
TUN-EMD1115	Authorities Review and Comment of FS Pump Head Calculation	56	50%	28	11-Jan-19 A	23-Jul-19				
TUN-EMD1135	Authorities Review and Comment of Sprinkler Pump Head Calculation	56	50%	28	25-Jan-19 A	23-Jul-19				
Plumbing & Drainage System										
TUN-EMD1185	Authorities Review and Comment of Drainage Sump Pumps and Pump Pits Calculation	56	50%	28	27-Sep-18 A	23-Jul-19				
Tunnel Lighting System										
TUN-EMD1075	Authorities Review and Comment of Design Proposal of Tunnel Lighting System (TLS)	56	50%	28	29-Aug-18 A	23-Jul-19				
TUN-EMD1095	Authorities Review and Comment of Tunnel Lighting Lux Calculation	56	50%	28	31-Dec-18 A	23-Jul-19				
CCMS, TCS and ELV System										
ELV-EMD1015	Authorities Review and Comment of System Design for Toll Control system	56	50%	28	27-Jul-18 A	23-Jul-19				
ELV-EMD1035	Authorities Review and Comment of System Design for CMCS	56	50%	28	26-Sep-18 A	23-Jul-19				
ELV-EMD1055	Authorities Review and Comment of System Design for other ELV systems	56	50%	28	02-Oct-18 A	23-Jul-19				
Major Material Submission & Approval										
GEN-EMM1020	Authorities Review and Comment of Technical Info. - Miscellaneous 1st fix Materials/ Equipment	28	50%	14	31-May-18 A	06-Jul-19				
GEN-EMM1050	Authorities Review and Comment of Technical Info. - Miscellaneous 2nd fix Materials/ Equipment	28	50%	14	20-May-18 A	06-Jul-19				
GEN-EMM1080	Authorities Review and Comment of Technical Info. - Miscellaneous final fix Materials/ Equipment	28	50%	14	02-Jul-18 A	06-Jul-19				
MVAC System										
MVAC-EMM1015	Authorities Review and Comment of Technical Info. - Chiller	56	50%	28	14-Jun-18 A	23-Jul-19				
MVAC-EMM1035	Authorities Review and Comment of Technical Info. - Chilled Water Pump	56	50%	28	12-Jun-18 A	23-Jul-19				
MVAC-EMM1055	Authorities Review and Comment of Technical Info. - Cooling Tower	56	50%	28	11-Jun-18 A	23-Jul-19				
MVAC-EMM1075	Authorities Review and Comment of Technical Info. - Computer Room AC (CRAC) Unit	56	50%	28	19-Jul-18 A	23-Jul-19				
MVAC-EMM1095	Authorities Review and Comment of Technical Info. - AHU & PAU	56	50%	28	10-Sep-18 A	23-Jul-19				
MVAC-EMM1115	Authorities Review and Comment of Technical Info. - Staircase Pressurization Fan	56	50%	28	17-Jul-18 A	23-Jul-19				
Electrical System										
ELE-EMM1075	Authorities Review and Comment of Technical Info. - HV Cables	56	50%	28	17-Sep-18 A	23-Jul-19				
ELE-EMM1155	Authorities Review and Comment of Technical Info. - UPS and Battery	28	50%	14	26-Nov-18 A	06-Jul-19				
ELE-EMM1175	Authorities Review and Comment of Technical Info. - MCB & MCCB & Distribution Board	28	50%	14	04-Dec-18 A	06-Jul-19				
ELE-EMM1215	ER Review and Approval of Technical Info. - PV System	13	50%	7	04-Apr-19 A	27-Jun-19				
ELE-EMM1225	Authorities Review and Comment of Technical Info. - PV System	56	50%	28	05-Mar-19 A	23-Jul-19				
Fire Service System										
FS-EMM1015	Authorities Review and Comment of Technical Info. - FM200	56	50%	28	20-Aug-18 A	23-Jul-19				
FS-EMM1095	Authorities Review and Comment of Technical Info. - FR/ HR system	56	50%	28	24-Sep-18 A	23-Jul-19				
FS-EMM1115	Authorities Review and Comment of Technical Info. - Gas detection	56	50%	28	05-Dec-18 A	23-Jul-19				
Plumbing & Drainage System										
PD-EMM1015	Authorities Review and Comment of Technical Info. - Sump Pump	56	50%	28	25-Oct-18 A	23-Jul-19				
PD-EMM1035	Authorities Review and Comment of Technical Info. - Hot Water System	56	50%	28	11-Nov-18 A	23-Jul-19				
PD-EMM1055	Authorities Review and Comment of Technical Info. - LMCP (PD)	56	50%	28	16-Jan-19 A	23-Jul-19				
Tunnel Ventilation System										
TVS-EMM1035	Authorities Review and Comment of Technical Info. - Pressurization Fan	56	50%	28	19-Jul-18 A	23-Jul-19				
TVS-EMM1105	Authorities Review and Comment of Technical Info. - AQMS Equipment	56	50%	28	29-Oct-18 A	23-Jul-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 4/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
TVS-EMM1155	Authorities Review and Comment of Technical Info. - MFSD	56	50%	28	26-Jul-18 A	23-Jul-19				
Tunnel and Road Lighting System										
TRLS-EMM1035	Authorities Review and Comment of Technical Info. - Road Lighting Fitting	56	50%	28	09-Oct-18 A	23-Jul-19				
CCMS, TCS and ELV System										
ELV-EMM1013	ER Review and Approval of Technical Info. - CMCS Equipment	40	85%	6	22-Jan-19 A	26-Jun-19				
ELV-EMM1020	Authorities Review and Comment of Technical Info. - CMCS Equipment	56	50%	28	09-Oct-18 A	23-Jul-19				
ELV-EMM1040	ER Review and Approval of Technical Info. - TCS Equipment	40	85%	6	28-Dec-18 A	26-Jun-19				
ELV-EMM1050	Authorities Review and Comment of Technical Info. - TCS Equipment	56	50%	28	09-Oct-18 A	23-Jul-19				
ELV-EMM1073	ER Review and Approval of Technical Info. - other ELV Equipment	40	85%	6	19-Mar-19 A	26-Jun-19				
ELV-EMM1080	Authorities Review and Comment of Technical Info. - other ELV Equipment	56	50%	28	15-Oct-18 A	23-Jul-19				
Drawing Submission & Approval										
Satellite Control Building										
Individual Shop Drawing										
SCB-ISD1010	ER Review and Comment of SCB ISD 1st batch	12	95%	1	11-Aug-18 A	20-Jun-19				
SCB-ISD1020	Preparation and Resubmission of SCB ISD 1st batch	12	95%	1	04-Jan-19 A	21-Jun-19				
SCB-ISD1030	ER Review and Approval of SCB ISD 1st batch	7	95%	0	04-Jan-19 A	21-Jun-19				
SCB-ISD1040	Authorities Review and Comment of SCB ISD 1st batch	28	50%	14	10-Aug-18 A	06-Jul-19				
SCB-ISD1060	ER Review and Comment of SCB ISD 2nd batch	12	95%	1	11-Aug-18 A	20-Jun-19				
SCB-ISD1070	Preparation and Resubmission of SCB ISD 2nd batch	12	95%	1	04-Jan-19 A	21-Jun-19				
SCB-ISD1080	ER Review and Approval of SCB ISD 2nd batch	7	95%	0	04-Jan-19 A	21-Jun-19				
SCB-ISD1090	Authorities Review and Comment of SCB ISD 2nd batch	28	50%	14	10-Aug-18 A	06-Jul-19				
Custom & Excise Department Building										
Individual Shop Drawing										
CEDB-ISD1040	Authorities Review and Comment of C&EDB ISD 1st batch	28	50%	14	06-Sep-18 A	06-Jul-19				
CEDB-ISD1090	Authorities Review and Comment of C&EDB ISD 2nd batch	28	50%	14	06-Sep-18 A	06-Jul-19				
South Ventilation Building										
Individual Shop Drawing										
SVB-ISD1030	ER Review and Approval of SVB ISD 1st batch	7	50%	4	08-Mar-19 A	24-Jun-19				
SVB-ISD1080	ER Review and Approval of SVB ISD 2nd batch	7	50%	4	08-Mar-19 A	24-Jun-19				
Structural, Electrical & Mechanical Drawing										
SVB-SEM2020	Preparation and Resubmission of SVB SEM	12	50%	6	10-Apr-19 A	26-Jun-19				
SVB-SEM2030	ER Review and Approval of SVB SEM	7	0%	7	27-Jun-19	05-Jul-19				
Tunnel										
Individual Shop Drawing										
TUN-ISD1060	ER Review and Comment of Tunnel ISD 2nd batch	30	85%	5	16-Aug-18 A	25-Jun-19				
TUN-ISD1070	Preparation and Resubmission of Tunnel ISD 2nd batch	30	85%	5	16-Feb-19 A	29-Jun-19				
TUN-ISD1080	ER Review and Approval of Tunnel ISD 2nd batch	15	85%	2	29-Aug-18 A	04-Jul-19				
TUN-ISD1090	Authorities Review and Comment of Tunnel ISD 2nd batch	28	50%	14	16-Aug-18 A	06-Jul-19				
TUN-ISD1110	ER Review and Comment of Tunnel ISD 3rd batch	30	0%	30	20-Jun-19	25-Jul-19				
TUN-ISD1120	Preparation and Resubmission of Tunnel ISD 3rd batch	30	0%	30	26-Jul-19	29-Aug-19				
TUN-ISD1130	ER Review and Approval of Tunnel ISD 3rd batch	15	0%	15	30-Aug-19	17-Sep-19				
TUN-ISD1140	Authorities Review and Comment of Tunnel ISD 3rd batch	28	50%	14	10-Dec-18 A	06-Jul-19				
TUN-ISD1160	ER Review and Comment of Tunnel ISD 4th batch	30	0%	30	20-Jun-19	25-Jul-19				
TUN-ISD1170	Preparation and Resubmission of Tunnel ISD 4th batch	30	0%	30	26-Jul-19	29-Aug-19				
TUN-ISD1180	ER Review and Approval of Tunnel ISD 4th batch	15	0%	15	30-Aug-19	17-Sep-19				
TUN-ISD1190	Authorities Review and Comment of Tunnel ISD 4th batch	28	50%	14	31-Oct-18 A	06-Jul-19				
Fire Services Department Building										
Individual Shop Drawing										

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 5/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
FSDB-ISD1040	Authorities Review and Comment of FSDB ISD 1st batch	28	50%	14	05-Sep-18 A	06-Jul-19				
FSDB-ISD1090	Authorities Review and Comment of FSDB ISD 2nd batch	28	50%	14	05-Sep-18 A	06-Jul-19				
Vehicular Underpass										
<i>Individual Shop Drawing</i>										
VU-ISD1080	ER Review and Approval of Vehicular Underpass ISD 2nd batch	7	50%	4	19-May-19 A	24-Jun-19				
VU-ISD1090	Authorities Review and Comment of Vehicular Underpass ISD 2nd batch	28	50%	14	02-Apr-19 A	06-Jul-19				
North Ventilation Building										
<i>Individual Shop Drawing</i>										
NVB-ISD1090	Authorities Review and Approval of NVB ISD - 2nd batch	28	50%	14	27-Sep-18 A	06-Jul-19				
E&M Procurement										
Design Related Procurement										
<i>Toll Control Building</i>										
CCMS, TCS and ELV System										
TCB-PO1150	Place Order - TCS Equipment	12	0%	12	27-Jun-19	11-Jul-19				
<i>Vehicular Underpass</i>										
Fire Service System										
VU-PO1040	Place Order - Gas detection	12	100%	0	30-May-19 A	30-May-19				
<i>Tunnel</i>										
Fire Service System										
TUN-PO1015	Place Order - Gas detection	12	100%	0	30-May-19 A	30-May-19				
E&M Manufacture & Delivery										
<i>Toll Control Building</i>										
MVAC System										
TCB-MD1010	Manufacture & Delivery to HK - Chiller	150	85.67%	22	07-Mar-19 A	11-Jul-19				
TCB-MD1020	Manufacture & Delivery to HK - Chilled Water Pump	100	93%	7	06-Mar-19 A	26-Jun-19				
TCB-MD1030	Manufacture & Delivery to HK - Computer Room Air Conditioning (CRAC) Unit	120	76.67%	28	15-May-19 A	17-Jul-19				
TCB-MD1040	Manufacture & Delivery to HK - Cooling Tower (R/F)	100	93%	7	06-Mar-19 A	26-Jun-19				
TCB-MD1050	Manufacture & Delivery to HK - AHU & PAU	90	71.11%	26	25-May-19 A	15-Jul-19				
Electrical System										
TCB-MD1060	Manufacture - LV Switchboard	86	86.05%	12	02-Apr-19 A	01-Jul-19				
TCB-MD1062	FAT - LV Switchboard	10	0%	10	02-Jul-19	11-Jul-19				
TCB-MD1065	Shipping to HK - LV Switchboard	14	0%	14	12-Jul-19	25-Jul-19				
TCB-MD1070	Manufacture - Generator	118	61.27%	46	02-Apr-19 A	04-Aug-19				
TCB-MD1072	FAT - Generator	4	0%	4	04-Aug-19	08-Aug-19				
TCB-MD1075	Shipping to HK - Generator	28	0%	28	08-Aug-19	05-Sep-19				
TCB-MD1080	Manufacture - UPS and Battery	53	75%	13	19-Mar-19 A	03-Jul-19				
TCB-MD1082	FAT - UPS and Battery	10	0%	10	03-Jul-19	13-Jul-19				
TCB-MD1085	Shipping to HK - UPS and Battery	42	0%	42	13-Jul-19	24-Aug-19				
TCB-MD1090	Manufacture & Delivery to HK - MCB & MCCB and Distribution Board	60	90%	6	04-Mar-19 A	25-Jun-19				
TCB-MD1100	Manufacture & Delivery to HK - LV Cables	120	85.83%	17	20-Nov-18 A	06-Jul-19				
TCB-MD1280	Manufacture & Delivery to HK - PV System Equipment	60	0%	60	21-Jul-19	18-Sep-19				
Fire Service System										
TCB-MD1150	Manufacture & Delivery to HK - FM200	150	60.67%	59	24-Dec-18 A	17-Aug-19				
TCB-MD1160	Manufacture & Delivery to HK - AFA System	100	91%	9	02-Mar-19 A	28-Jun-19				
TCB-MD1170	Manufacture & Delivery to HK - FS Pump	120	92.5%	9	19-Mar-19 A	28-Jun-19				
TCB-MD1180	Manufacture & Delivery to HK - FR/ HR system	90	90%	9	02-Mar-19 A	28-Jun-19				
TCB-MD1190	Manufacture & Delivery to HK - LMCP (FS)	60	51.67%	29	20-May-19 A	18-Jul-19				
Plumbing & Drainage System										

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 6/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
TCB-MD1110	Manufacture & Delivery to HK - Sump Pump	120	85.83%	17	29-Mar-19 A	06-Jul-19				
TCB-MD1120	Manufacture & Delivery to HK - Hot Water System	120	20%	96	04-Jun-19 A	23-Sep-19				
TCB-MD1130	Manufacture & Delivery to HK - LMCP (PD)	60	51.67%	29	20-May-19 A	18-Jul-19				
TCB-MD1140	Manufacture & Delivery to HK - Water Pump	90	94.44%	5	29-Mar-19 A	24-Jun-19				
Lift System										
TCB-MD1000	Manufacture & Delivery to HK - Lift System	120	75.83%	29	03-Apr-19 A	18-Jul-19				
CCMS, TCS and ELV System										
TCB-MD1200	Manufacture - CMCS Equipment	62	45.16%	34	20-Apr-19 A	30-Jul-19				
TCB-MD1202	FAT - CMCS Equipment	7	0%	7	31-Jul-19	06-Aug-19				
TCB-MD1205	Shipping to HK - CMCS Equipment	14	0%	14	07-Aug-19	20-Aug-19				
TCB-MD1210	Manufacture - TCS Equipment	82	0%	82	12-Jul-19	01-Oct-19				
TCB-MD1220	Manufacture & Delivery to HK - other ELV Equipment	83	38.55%	51	18-Jun-19 A	16-Aug-19				
Administration Building										
Electrical System										
ADB-MD1070	Manufacture - LV Switchboard	86	86.05%	12	02-Apr-19 A	01-Jul-19				
ADB-MD1072	FAT - LV Switchboard	10	0%	10	02-Jul-19	11-Jul-19				
ADB-MD1075	Shipping to HK - LV Switchboard	14	0%	14	12-Jul-19	25-Jul-19				
ADB-MD1080	Manufacture - Generator	118	61.27%	46	02-Apr-19 A	04-Aug-19				
ADB-MD1082	FAT - Generator	4	0%	4	04-Aug-19	08-Aug-19				
ADB-MD1085	Shipping to HK - Generator	28	0%	28	08-Aug-19	05-Sep-19				
ADB-MD1090	Manufacture - UPS and Battery	53	20%	42	24-May-19 A	01-Aug-19				
ADB-MD1092	FAT - UPS and Battery	10	0%	10	01-Aug-19	11-Aug-19				
ADB-MD1095	Shipping to HK - UPS and Battery	42	0%	42	11-Aug-19	22-Sep-19				
ADB-MD1110	Manufacture & Delivery to HK - LV Cables	120	85.83%	17	20-Nov-18 A	06-Jul-19				
ADB-MD1310	Manufacture & Delivery to HK - PV System Equipment	60	0%	60	21-Jul-19	18-Sep-19				
MVAC System										
ADB-MD1010	Manufacture & Delivery to HK - Chiller	150	85.67%	22	06-Mar-19 A	11-Jul-19				
ADB-MD1020	Manufacture & Delivery to HK - Chilled Water Pump	100	91%	9	06-Mar-19 A	28-Jun-19				
ADB-MD1030	Manufacture & Delivery to HK - Computer Room Air Conditioning (CRAC) Unit	120	50.83%	59	15-May-19 A	17-Aug-19				
ADB-MD1040	Manufacture & Delivery to HK - AHU & PAU	90	27.78%	65	25-May-19 A	23-Aug-19				
ADB-MD1050	Manufacture & Delivery to HK - Cooling Tower	100	57%	43	06-Mar-19 A	01-Aug-19				
Fire Service System										
ADB-MD1160	Manufacture & Delivery to HK - FM200	150	80.67%	29	24-Dec-18 A	18-Jul-19				
ADB-MD1170	Manufacture & Delivery to HK - AFA System	100	91%	9	02-Mar-19 A	28-Jun-19				
ADB-MD1180	Manufacture & Delivery to HK - FS Pump	120	95.83%	5	19-Mar-19 A	24-Jun-19				
ADB-MD1190	Manufacture & Delivery to HK - FR/ HR system	90	94.44%	5	02-Mar-19 A	24-Jun-19				
ADB-MD1200	Manufacture & Delivery to HK - LMCP (FS)	60	51.67%	29	20-May-19 A	18-Jul-19				
Plumbing & Drainage System										
ADB-MD1130	Manufacture & Delivery to HK - Hot Water System	120	20%	96	04-Jun-19 A	23-Sep-19				
ADB-MD1140	Manufacture & Delivery to HK - LMCP (PD)	60	51.67%	29	20-May-19 A	18-Jul-19				
ADB-MD1150	Manufacture & Delivery to HK - Water Pump	90	84.44%	14	29-Mar-19 A	03-Jul-19				
CCMS and ELV System										
ADB-MD1210	Manufacture - CMCS Equipment	62	45.16%	34	20-Apr-19 A	30-Jul-19				
ADB-MD1212	FAT - CMCS Equipment	7	0%	7	31-Jul-19	06-Aug-19				
ADB-MD1215	Shipping to HK - CMCS Equipment	14	0%	14	07-Aug-19	20-Aug-19				
ADB-MD1220	Manufacture & Delivery to HK - other ELV Equipment	83	38.55%	51	18-Jun-19 A	16-Aug-19				
Lift System										
ADB-MD1000	Manufacture & Delivery to HK - Lift System	120	50.83%	59	03-Apr-19 A	17-Aug-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 7/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
North Ventilation Building											
Electrical System											
NVB-MD1025	Shipping to HK - HV Switchboard	14	10%	13	19-Jun-19 A	02-Jul-19					
NVB-MD1035	Shipping to HK - HV Cables	14	64.29%	5	10-Jun-19 A	24-Jun-19					
NVB-MD1040	Manufacture - LV Switchboard	86	86.05%	12	02-Apr-19 A	01-Jul-19					
NVB-MD1042	FAT - LV Switchboard	10	0%	10	02-Jul-19	11-Jul-19					
NVB-MD1045	Shipping to HK - LV Switchboard	14	0%	14	12-Jul-19	25-Jul-19					
NVB-MD1050	Manufacture - Generator	118	61.27%	46	02-Apr-19 A	04-Aug-19					
NVB-MD1052	FAT - Generator	4	0%	4	04-Aug-19	08-Aug-19					
NVB-MD1055	Shipping to HK - Generator	28	0%	28	08-Aug-19	05-Sep-19					
NVB-MD1060	Manufacture - UPS and Battery	53	75%	13	19-Mar-19 A	03-Jul-19					
NVB-MD1062	FAT - UPS and Battery	10	0%	10	03-Jul-19	13-Jul-19					
NVB-MD1065	Shipping to HK - UPS and Battery	42	0%	42	13-Jul-19	24-Aug-19					
NVB-MD1095	Shipping to HK - LV Cables	14	64.29%	5	10-Jun-19 A	24-Jun-19					
MVAC System											
NVB-MD1200	Shipping to HK - Tunnel Ventilation Fan	45	20%	36	16-Jun-19 A	25-Jul-19					
NVB-MD1210	Manufacture & Delivery to HK - Staircase Pressurization Fan	60	0%	60	20-Jun-19	18-Aug-19					
Fire Service System											
NVB-MD1130	Manufacture & Delivery to HK - FM200	150	80.67%	29	24-Dec-18 A	18-Jul-19					
NVB-MD1140	Manufacture & Delivery to HK - AFA System	100	91%	9	02-Mar-19 A	28-Jun-19					
NVB-MD1150	Manufacture & Delivery to HK - FR/ HR system	90	94.44%	5	02-Mar-19 A	24-Jun-19					
NVB-MD1170	Manufacture & Delivery to HK - LMCP (FS)	60	51.67%	29	20-May-19 A	18-Jul-19					
Plumbing & Drainage System											
NVB-MD1100	Manufacture & Delivery to HK - Sump Pump	120	85.83%	17	29-Mar-19 A	06-Jul-19					
NVB-MD1110	Manufacture & Delivery to HK - LMCP (PD)	60	51.67%	29	20-May-19 A	18-Jul-19					
NVB-MD1120	Manufacture & Delivery to HK - Water Pump	90	79.44%	19	29-Mar-19 A	08-Jul-19					
CCMS and ELV System											
NVB-MD1220	Manufacture - CMCS Equipment	62	45.16%	34	20-Apr-19 A	30-Jul-19					
NVB-MD1222	FAT - CMCS Equipment	7	0%	7	31-Jul-19	06-Aug-19					
NVB-MD1225	Shipping to HK - CMCS Equipment	14	0%	14	07-Aug-19	20-Aug-19					
NVB-MD1230	Manufacture - other ELV Equipment	62	53%	29	18-Jun-19 A	26-Jul-19					
NVB-MD1232	FAT - other ELV Equipment	7	0%	7	26-Jul-19	02-Aug-19					
NVB-MD1235	Shipping to HK - other ELV Equipment	14	0%	14	02-Aug-19	16-Aug-19					
Lift System											
NVB-MD1000	Manufacture & Delivery to HK - Lift System	120	75.83%	29	03-Apr-19 A	18-Jul-19					
Maintenance Depot											
Electrical System											
MD-MD1010	Manufacture - Generator	118	61.27%	46	02-Apr-19 A	04-Aug-19					
MD-MD1012	FAT - Generator	4	0%	4	04-Aug-19	08-Aug-19					
MD-MD1015	Shipping to HK - Generator	28	0%	28	08-Aug-19	05-Sep-19					
MD-MD1020	Manufacture - LV Switchboard	86	86.05%	12	02-Apr-19 A	01-Jul-19					
MD-MD1022	FAT - LV Switchboard	10	0%	10	02-Jul-19	11-Jul-19					
MD-MD1025	Shipping to HK - LV Switchboard	14	0%	14	12-Jul-19	25-Jul-19					
MD-MD1030	Manufacture & Delivery to HK - MCB & MCCB and Distribution Board	60	91.67%	5	04-Mar-19 A	24-Jun-19					
MD-MD1040	Manufacture & Delivery to HK - LV Cables	120	75.83%	29	20-Nov-18 A	18-Jul-19					
MVAC System											
MD-MD1000	Manufacture & Delivery to HK - AHU & PAU	90	71.11%	26	25-May-19 A	15-Jul-19					
Fire Service System											

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 8/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
MD-MD1080	Manufacture & Delivery to HK - FM200	150	80.67%	29	24-Dec-18 A	18-Jul-19				
MD-MD1090	Manufacture & Delivery to HK - FS Pump	120	95.83%	5	19-Mar-19 A	24-Jun-19				
MD-MD1100	Manufacture & Delivery to HK - AFA System	100	91%	9	02-Mar-19 A	28-Jun-19				
MD-MD1110	Manufacture & Delivery to HK - LMCP (FS)	60	51.67%	29	20-May-19 A	18-Jul-19				
MD-MD1120	Manufacture & Delivery to HK - FR/ HR system	90	94.44%	5	02-Mar-19 A	24-Jun-19				
CCMS and ELV System										
MD-MD1130	Manufacture - CMCS Equipment	62	45.16%	34	20-May-19 A	30-Jul-19				
MD-MD1132	FAT - CMCS Equipment	7	0%	7	31-Jul-19	06-Aug-19				
MD-MD1135	Shipping to HK - CMCS Equipment	14	0%	14	07-Aug-19	20-Aug-19				
MD-MD1140	Manufacture & Delivery to HK - other ELV Equipment	83	38.55%	51	18-Jun-19 A	16-Aug-19				
Plumbing & Drainage System										
MD-MD1050	Manufacture & Delivery to HK - Sump Pump	120	85.83%	17	29-Mar-19 A	06-Jul-19				
MD-MD1060	Manufacture & Delivery to HK - Water Pump	90	79.44%	19	29-Mar-19 A	08-Jul-19				
MD-MD1070	Manufacture & Delivery to HK - LMCP (PD)	60	51.67%	29	20-May-19 A	18-Jul-19				
Satellite Control Building										
SCB-MD1175	Manufacture & Delivery to HK - Miscellaneous 1st fix Materials/ Equipment	45	0%	45	20-Jun-19	03-Aug-19				
SCB-MD1185	Manufacture & Delivery to HK - Miscellaneous 2nd fix Materials/ Equipment	45	0%	45	27-Jun-19	10-Aug-19				
SCB-MD1195	Manufacture & Delivery to HK - Miscellaneous final fix Materials/ Equipment	45	0%	45	13-Jul-19	26-Aug-19				
Electrical System										
SCB-MD1020	Manufacture - Generator	118	31.27%	81	17-Apr-19 A	09-Sep-19				
SCB-MD1022	FAT - Generator	4	0%	4	09-Sep-19	13-Sep-19				
SCB-MD1025	Shipping to HK - Generator	28	0%	28	13-Sep-19	11-Oct-19				
SCB-MD1030	Manufacture - UPS and Battery	53	20%	42	26-Mar-19 A	01-Aug-19				
SCB-MD1032	FAT - UPS and Battery	10	0%	10	01-Aug-19	11-Aug-19				
SCB-MD1035	Shipping to HK - UPS and Battery	42	0%	42	11-Aug-19	22-Sep-19				
SCB-MD1040	Manufacture - LV Switchboard	86	41.05%	51	17-Apr-19 A	09-Aug-19				
SCB-MD1042	FAT - LV Switchboard	10	0%	10	09-Aug-19	19-Aug-19				
SCB-MD1045	Shipping to HK - LV Switchboard	14	0%	14	19-Aug-19	02-Sep-19				
SCB-MD1050	Manufacture & Delivery to HK - MCB & MCCB and Distribution Board	60	0%	60	28-Jul-19	25-Sep-19				
SCB-MD1060	Manufacture & Delivery to HK - LV Cables	120	35.83%	77	20-Nov-18 A	11-Sep-19				
MVAC System										
SCB-MD1010	Manufacture & Delivery to HK - Computer Room Air Conditioning (CRAC) Unit	120	25.83%	89	25-May-19 A	16-Sep-19				
Fire Service System										
SCB-MD1100	Manufacture & Delivery to HK - FM200	150	40%	90	20-May-19 A	17-Sep-19				
SCB-MD1110	Manufacture & Delivery to HK - FS Pump	120	25.83%	89	19-Mar-19 A	16-Sep-19				
SCB-MD1120	Manufacture & Delivery to HK - AFA System	100	0%	100	28-Jul-19	04-Nov-19				
SCB-MD1130	Manufacture & Delivery to HK - LMCP (FS)	60	0%	60	08-Sep-19	06-Nov-19				
SCB-MD1140	Manufacture & Delivery to HK - FR/ HR system	90	0%	90	18-Sep-19	16-Dec-19				
Plumbing & Drainage System										
SCB-PO1120	Manufacture & Delivery to HK - LMCP (PD)	60	0%	60	08-Sep-19	06-Nov-19				
SCB-PO1130	Manufacture & Delivery to HK - Water Pump	90	34.44%	59	29-Mar-19 A	17-Aug-19				
CCMS and ELV System										
SCB-MD1150	Manufacture - CMCS Equipment	62	0%	62	31-Jul-19	30-Sep-19				
SCB-MD1160	Manufacture & Delivery to HK - other ELV Equipment	83	0%	83	27-Jun-19	17-Sep-19				
Lift System										
SCB-MD1000	Manufacture & Delivery to HK - Lift System	120	45.83%	65	03-Apr-19 A	23-Aug-19				
Custom & Excise Department Building										
CEDB-MD1195	Manufacture & Delivery to HK - Miscellaneous 1st fix Materials/ Equipment	45	0%	45	20-Jun-19	03-Aug-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 9/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
CEDB-MD1205	Manufacture & Delivery to HK - Miscellaneous 2nd fix Materials/ Equipment	45	0%	45	10-Jul-19	23-Aug-19				
CEDB-MD1215	Manufacture & Delivery to HK - Miscellaneous final fix Materials/ Equipment	45	0%	45	25-Jul-19	07-Sep-19				
Electrical System										
CEDB-MD1020	Manufacture - Generator	118	46.27%	63	17-Apr-19 A	22-Aug-19				
CEDB-MD1022	FAT - Generator	4	0%	4	22-Aug-19	26-Aug-19				
CEDB-MD1025	Shipping to HK - Generator	28	0%	28	26-Aug-19	23-Sep-19				
CEDB-MD1030	Manufacture - UPS and Battery	53	20%	42	26-Mar-19 A	01-Aug-19				
CEDB-MD1032	FAT - UPS and Battery	10	0%	10	01-Aug-19	11-Aug-19				
CEDB-MD1035	Shipping to HK - UPS and Battery	42	0%	42	11-Aug-19	22-Sep-19				
CEDB-MD1040	Manufacture - LV Switchboard	86	41.05%	51	17-Apr-19 A	09-Aug-19				
CEDB-MD1042	FAT - LV Switchboard	10	0%	10	09-Aug-19	19-Aug-19				
CEDB-MD1045	Shipping to HK - LV Switchboard	14	0%	14	19-Aug-19	02-Sep-19				
CEDB-MD1050	Manufacture & Delivery to HK - LV Cables	120	35.83%	77	20-Nov-18 A	11-Sep-19				
CEDB-MD1060	Manufacture & Delivery to HK - MCB & MCCB and Distribution Board	60	0%	60	28-Jun-19	26-Aug-19				
MVAC System										
CEDB-MD1010	Manufacture & Delivery to HK - AHU & PAU	90	0%	90	20-Jun-19	17-Sep-19				
Fire Service System										
CEDB-MD1090	Manufacture & Delivery to HK - FM200	150	0%	150	20-Jun-19	16-Nov-19				
CEDB-MD1100	Manufacture & Delivery to HK - FS Pump	120	25.83%	89	19-Mar-19 A	16-Sep-19				
CEDB-MD1110	Manufacture & Delivery to HK - AFA System	100	0%	100	20-Jun-19	27-Sep-19				
CEDB-MD1120	Manufacture & Delivery to HK - LMCP (FS)	60	0%	60	11-Jul-19	08-Sep-19				
CEDB-MD1130	Manufacture & Delivery to HK - FR/ HR system	90	0%	90	24-Jul-19	21-Oct-19				
Plumbing & Drainage System										
CEDB-MD1070	Manufacture & Delivery to HK - LMCP (PD)	60	0%	60	20-Jun-19	18-Aug-19				
CEDB-MD1080	Manufacture & Delivery to HK - Water Pump	90	34.44%	59	29-Mar-19 A	01-Nov-19				
CCMS and ELV System										
CEDB-MD1170	Manufacture - CMCS Equipment	62	0%	62	25-Jul-19	24-Sep-19				
CEDB-MD1180	Manufacture & Delivery to HK - other ELV Equipment	83	0%	83	24-Jul-19	14-Oct-19				
Lift System										
CEDB-MD1000	Manufacture & Delivery to HK - Lift System	120	0%	120	20-Jun-19	17-Oct-19				
Fire Services Department Building										
FSDB-MD1155	Manufacture & Delivery to HK - Miscellaneous 1st fix Materials/ Equipment	45	0%	45	22-Jun-19	05-Aug-19				
FSDB-MD1165	Manufacture & Delivery to HK - Miscellaneous 2nd fix Materials/ Equipment	45	0%	45	27-Jun-19	10-Aug-19				
FSDB-MD1175	Manufacture & Delivery to HK - Miscellaneous final fix Materials/ Equipment	45	0%	45	13-Jul-19	26-Aug-19				
Electrical System										
FSDB-MD1000	Manufacture - Generator	118	46.27%	63	17-Apr-19 A	22-Aug-19				
FSDB-MD1002	FAT - Generator	4	0%	4	22-Aug-19	26-Aug-19				
FSDB-MD1005	Shipping to HK - Generator	28	0%	28	26-Aug-19	23-Sep-19				
FSDB-MD1010	Manufacture - UPS and Battery	53	20%	42	26-Mar-19 A	01-Aug-19				
FSDB-MD1012	FAT - UPS and Battery	10	0%	10	01-Aug-19	11-Aug-19				
FSDB-MD1015	Shipping to HK - UPS and Battery	42	0%	42	11-Aug-19	22-Sep-19				
FSDB-MD1020	Manufacture - LV Switchboard	86	41.05%	51	17-Apr-19 A	09-Aug-19				
FSDB-MD1022	FAT - LV Switchboard	10	0%	10	09-Aug-19	19-Aug-19				
FSDB-MD1025	Shipping to HK - LV Switchboard	14	0%	14	19-Aug-19	02-Sep-19				
FSDB-MD1030	Manufacture & Delivery to HK - LV Cables	120	35.83%	77	20-Nov-18 A	05-Oct-19				
FSDB-MD1040	Manufacture & Delivery to HK - MCB & MCCB and Distribution Board	60	0%	60	03-Aug-19	01-Oct-19				
Fire Service System										
FSDB-MD1090	Manufacture & Delivery to HK - FS Pump	120	0%	120	20-Jun-19	17-Oct-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 10/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
FSDB-MD1100	Manufacture & Delivery to HK - AFA System	100	0%	100	20-Jun-19	27-Sep-19				
FSDB-MD1110	Manufacture & Delivery to HK - LMCP (FS)	60	0%	60	21-Aug-19	19-Oct-19				
FSDB-MD1120	Manufacture & Delivery to HK - FR/ HR system	90	0%	90	05-Sep-19	03-Dec-19				
FSDB-MD1185	Manufacture & Delivery to HK - FM200	150	0%	150	20-Jun-19	16-Nov-19				
Plumbing & Drainage System										
FSDB-MD1060	Manufacture & Delivery to HK - Water Pump	90	0%	90	06-Aug-19	03-Nov-19				
FSDB-MD1070	Manufacture & Delivery to HK - LMCP (PD)	60	0%	60	10-Aug-19	08-Oct-19				
CCMS and ELV System										
FSDB-MD1130	Manufacture - CMCS Equipment	62	0%	62	23-Aug-19	23-Oct-19				
FSDB-MD1140	Manufacture & Delivery to HK - other ELV Equipment	83	0%	83	27-Aug-19	17-Nov-19				
South Ventilation Building										
SVB-MD1225	Manufacture & Delivery to HK - Miscellaneous 1st fix Materials/ Equipment	45	50%	23	21-Mar-19 A	12-Jul-19				
SVB-MD1235	Manufacture & Delivery to HK - Miscellaneous 2nd fix Materials/ Equipment	45	0%	45	20-Jun-19	03-Aug-19				
SVB-MD1245	Manufacture & Delivery to HK - Miscellaneous final fix Materials/ Equipment	45	0%	45	20-Jun-19	03-Aug-19				
Electrical System										
SVB-MD1000	Manufacture - Generator	118	29.27%	83	17-Apr-19 A	11-Sep-19				
SVB-MD1002	FAT - Generator	4	0%	4	11-Sep-19	15-Sep-19				
SVB-MD1005	Shipping to HK - Generator	28	0%	28	15-Sep-19	13-Oct-19				
SVB-MD1010	Manufacture - UPS and Battery	53	20%	42	26-Mar-19 A	01-Aug-19				
SVB-MD1012	FAT - UPS and Battery	10	0%	10	01-Aug-19	11-Aug-19				
SVB-MD1015	Shipping to HK - UPS and Battery	42	0%	42	11-Aug-19	22-Sep-19				
SVB-MD1020	Manufacture - HV/LV Transformer	92	38.7%	56	16-May-19 A	15-Aug-19				
SVB-MD1022	FAT - HV/LV Transformer	14	0%	14	15-Aug-19	29-Aug-19				
SVB-MD1025	Shipping to HK - HV/LV Transformer	14	0%	14	29-Aug-19	12-Sep-19				
SVB-MD1030	Manufacture - LV Switchboard	86	39.05%	52	17-Apr-19 A	11-Aug-19				
SVB-MD1032	FAT - LV Switchboard	10	0%	10	11-Aug-19	21-Aug-19				
SVB-MD1035	Shipping to HK - LV Switchboard	14	0%	14	21-Aug-19	04-Sep-19				
SVB-MD1040	Manufacture - HV Switchboard	92	38.7%	56	16-May-19 A	15-Aug-19				
SVB-MD1042	FAT - HV Switchboard	14	0%	14	15-Aug-19	29-Aug-19				
SVB-MD1045	Shipping to HK - HV Switchboard	14	0%	14	29-Aug-19	12-Sep-19				
SVB-MD1050	Manufacture & Delivery to HK - HV Cables	120	80%	24	20-May-19 A	13-Jul-19				
SVB-MD1060	Manufacture & Delivery to HK - Busduct	120	0%	120	20-Jun-19	17-Oct-19				
SVB-MD1070	Manufacture & Delivery to HK - LV Cables	120	35.83%	77	20-Nov-18 A	04-Sep-19				
SVB-MD1080	Manufacture & Delivery to HK - MCB & MCCB and Distribution Board	60	0%	60	20-Jun-19	18-Aug-19				
MVAC System										
SVB-MD1170	Manufacture - Tunnel Ventilation Fan	180	52.22%	86	17-May-19 A	13-Sep-19				
SVB-MD1175	Shipping to HK - Tunnel Ventilation Fan	45	0%	45	14-Sep-19	28-Oct-19				
SVB-MD1180	Manufacture & Delivery to HK - Staircase Pressurization Fan	60	0%	60	20-Jun-19	18-Aug-19				
Fire Service System										
SVB-MD1120	Manufacture & Delivery to HK - FM200	150	80%	30	20-May-19 A	19-Jul-19				
SVB-MD1130	Manufacture & Delivery to HK - FS Pump	120	25.83%	89	19-Mar-19 A	16-Sep-19				
SVB-MD1140	Manufacture & Delivery to HK - AFA System	100	0%	100	20-Jun-19	27-Sep-19				
SVB-MD1150	Manufacture & Delivery to HK - FR/ HR system	90	0%	90	20-Jun-19	17-Sep-19				
SVB-MD1160	Manufacture & Delivery to HK - LMCP (FS)	60	0%	60	20-Jun-19	18-Aug-19				
Plumbing & Drainage System										
SVB-MD1100	Manufacture & Delivery to HK - Water Pump	90	34.44%	59	29-Mar-19 A	17-Aug-19				
SVB-MD1110	Manufacture & Delivery to HK - LMCP (PD)	60	0%	60	20-Jun-19	18-Aug-19				
SVB-MD1255	Manufacture & Delivery to HK - Sump Pump	120	25.83%	89	29-Mar-19 A	16-Sep-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 11/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
CCMS and ELV System											
SVB-MD1200	Manufacture - CMCS Equipment	62	0%	62	27-Jun-19	27-Aug-19					
SVB-MD1202	FAT - CMCS Equipment	7	0%	7	28-Aug-19	03-Sep-19					
SVB-MD1205	Shipping to HK - CMCS Equipment	14	0%	14	04-Sep-19	17-Sep-19					
SVB-MD1210	Manufacture & Delivery to HK - other ELV Equipment	83	37.35%	52	18-Jun-19 A	17-Aug-19					
Lift System											
SVB-MD1190	Manufacture & Delivery to HK - Lift System	120	2.5%	117	17-Jun-19 A	14-Oct-19					
Vehicular Underpass											
VU-MD1000	Manufacture & Delivery to HK - Pressurization Fan	90	93.33%	6	15-Apr-19 A	25-Jun-19					
VU-MD1015	Shipping to HK- Jet Fan	14	0%	14	09-May-19 A	03-Jul-19					
VU-MD1030	Manufacture & Delivery to HK - Sump Pump	120	65.83%	41	02-Apr-19 A	30-Jul-19					
VU-MD1040	Manufacture & Delivery to HK - Water Pump	90	34.44%	59	20-May-19 A	17-Aug-19					
VU-MD1050	Manufacture & Delivery to HK - Gas detection	90	0%	90	20-Jun-19	17-Sep-19					
VU-MD1060	Manufacture - CMCS Equipment	62	35%	40	20-May-19 A	06-Aug-19					
VU-MD1062	FAT - CMCS Equipment	7	0%	7	06-Aug-19	13-Aug-19					
VU-MD1065	Shipping to HK - CMCS Equipment	21	0%	21	13-Aug-19	03-Sep-19					
VU-MD1070	Manufacture & Delivery to HK - other ELV Equipment	90	38.55%	55	18-Jun-19 A	21-Aug-19					
Tunnel											
TUN-MD1006	Manufacture - Tunnel Lighting System (3rd Batch)	90	10%	81	20-May-19 A	08-Sep-19					
TUN-MD1009	Manufacture - Tunnel Lighting System (4th Batch)	90	0%	90	20-Jun-19 A	17-Sep-19					
TUN-MD1015	Manufacture & Delivery to HK - Gas detection	90	0%	90	20-Jun-19	17-Sep-19					
TUN-MD1020	Manufacture & Delivery to HK - LHD system	90	84.44%	14	04-Apr-19 A	03-Jul-19					
TUN-MD1030	Manufacture & Delivery to HK - FS Pump	60	0%	60	20-Jun-19	18-Aug-19					
TUN-MD1040	Manufacture - CMCS Equipment	62	35%	40	20-May-19 A	06-Aug-19					
TUN-MD1042	FAT - CMCS Equipment	21	0%	21	06-Aug-19	27-Aug-19					
TUN-MD1045	Shipping to HK - CMCS Equipment	7	0%	7	27-Aug-19	03-Sep-19					
TUN-MD1050	Manufacture & Delivery to HK - other ELV Equipment	90	38.55%	55	18-Jun-19 A	21-Aug-19					
TUN-MD1060	Manufacture & Delivery to HK - Sump Pump	120	0%	120	20-Jun-19	17-Oct-19					
TUN-MD1070	Manufacture - AQMS Equipment	69	60%	28	20-May-19 A	17-Jul-19					
TUN-MD1080	FAT - AQMS Equipment	14	0%	14	17-Jul-19	31-Jul-19					
TUN-MD1090	Shipping to HK - AQMS Equipment	7	0%	7	31-Jul-19	07-Aug-19					
Approach Road											
AR-MD1000	Manufacture & Delivery to HK - Road Lighting Fitting	90	64.44%	32	21-Mar-19 A	21-Jul-19					
AR-MD1010	Manufacture - CMCS Equipment	62	35%	40	20-May-19 A	06-Aug-19					
AR-MD1015	FAT - CMCS Equipment	7	0%	7	06-Aug-19	13-Aug-19					
AR-MD1018	Shipping to HK - CMCS Equipment	14	0%	14	13-Aug-19	27-Aug-19					
AR-MD1020	Manufacture & Delivery to HK - other ELV Equipment	83	38.55%	51	18-Jun-19 A	17-Aug-19					
Key Date 1 - Toll Control Building (TCB) & TCCS Provision											
ABWF Works (for All)											
ATCB1010	Door and Window Frames	82	0%	82	04-Mar-19 A	25-Sep-19					
ATCB1052	ABWF Works to Office and Corridors 2/F	152	98.03%	3	12-Apr-19 A	22-Jun-19					
ATCB1080	ABWF Works to Toilets G/F	163	94.48%	9	27-Feb-19 A	29-Jun-19					
ATCB1081	ABWF Works to Toilets 1/F	163	94.48%	9	01-Mar-19 A	29-Jun-19					
ATCB1082	ABWF Works to Toilets 2/F	163	87.12%	21	12-Apr-19 A	15-Jul-19					
ATCB1110	Waterproofing and Roofing	47	93.62%	3	14-Jun-19 A	22-Jun-19					
ATCB1120	External Cladding and Wall Plastering	94	77.66%	21	01-Apr-19 A	15-Jul-19					
TCCS Provision											
TCB230	KD1 Achieved	0	100%	0		31-May-19					

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 12/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
Key Date 4 - E&M Works in Vehicular Underpass Area & TCSS Provision											
E&M Works											
VU120	Cable containment Installation	24	90%	2	22-Mar-19 A	22-Jun-19					
VU130	Post Drill and Bracket Fixing	18	50%	9	02-Apr-19 A	04-Jul-19					
VU200	Possess Portion XI	0	100%	0	31-May-19 A						
VU210	KD4 Achieved	0	0%	0		04-Jul-19					
Key Date 2 - Administration Building, Maintenance Depot, Kiosk N2, TCSS Provision											
Administration Building (ADB)											
Building Structure											
ADB200	Roof Slab	28	67.86%	9	23-May-19 A	29-Jun-19					
ADB210	Top Roof	11	0%	11	02-Jul-19	13-Jul-19					
ABWF Works (for All)											
AADB1130	Blockwork Walls	25	0%	25	20-Jun-19	19-Jul-19					
AADB1140	Door and Window Frames	19	0%	19	20-Jun-19	12-Jul-19					
AADB1150	ABWF Works to Plant Rooms G/F	52	40.38%	31	07-Jun-19 A	02-Aug-19					
AADB1151	ABWF Works to Plant Rooms 1/F	52	0%	52	29-Jun-19	29-Aug-19					
AADB1160	ABWF Works to Office and Corridors G/F	126	0%	126	27-Jun-19	25-Nov-19					
AADB1161	ABWF Works to Office and Corridors 1/F	126	0%	126	12-Jul-19	09-Dec-19					
AADB1170	ABWF Works to Toilets G/F	132	0%	132	27-Jun-19	02-Dec-19					
AADB1171	ABWF Works to Toilets 1/F	132	0%	132	12-Jul-19	16-Dec-19					
AADB1180	Waterproofing and Roofing	48	0%	48	05-Jul-19	29-Aug-19					
AADB1190	External Cladding and Wall Plastering	98	0%	98	05-Jul-19	30-Oct-19					
Provision for TCSS Installation											
ADB250	Cable Containment Installation to enable TCSS installation	74	0%	74	20-Jun-19	16-Sep-19					
Maintenance Depot											
ABWF Works (for All)											
AMD1000	Blockwork Walls	16	12.5%	14	06-Jun-19 A	06-Jul-19					
AMD1010	Door and Window Frames	10	0%	10	20-Jun-19	02-Jul-19					
AMD1020	ABWF Works to Plant Rooms	58	0%	58	21-Jun-19	28-Aug-19					
AMD1030	ABWF Works to Office and Corridors	132	0%	132	21-Jun-19	26-Nov-19					
AMD1040	ABWF Works to Toilets	144	0%	144	25-Jun-19	13-Dec-19					
AMD1050	Waterproofing and Roofing	51	0%	51	29-Jun-19	28-Aug-19					
AMD1060	External Cladding and Wall Plastering	98	0%	98	29-Jun-19	25-Oct-19					
Provision for TCSS Installation											
MD210	Cable Containment Installation to enable TCSS installation	62	0%	62	25-Jul-19	08-Oct-19					
Kiosk N2											
N2-130	ABWF Works to enable TCSS installation	18	0%	18	20-Jun-19	11-Jul-19					
N2-140	Cable Containment Installation to enable TCSS installation	19	0%	19	12-Jul-19	02-Aug-19					
Key Date 6 - E&M Works for Administration Building, Maintenance Depot, North Vent Building, Kiosk N2											
ABWF Works for Administration Building (Structure Completed under KD2)											
EADB110	ADB First Floor Completed with Scaffolding Removed	0	100%	0		01-Jun-19 A					
E&M Works for Administration Building											
Installation											
G/F											
ADB-EMGF1000	ABWF Works ready for E&M Mobilization to General Areas - G/F	0	0%	0	02-Jul-19						
ADB-EMGF1010	E&M Installation - 1st fix - G/F	46	0%	46	02-Jul-19	23-Aug-19					
ADB-EMGF1020	E&M Installation - 2nd fix - G/F	40	0%	40	02-Aug-19	18-Sep-19					
ADB-EMGF1030	E&M Installation - Final fix - G/F	40	0%	40	27-Aug-19	15-Oct-19					

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 13/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
ADB-EMGF1040	ABWF Works ready for E&M Mobilization to 11kV Swtich & Tx Room 1 - G/F	0	0%	0	04-Jul-19		◆			
ADB-EMGF1050	E&M Installation - 11kV Swtich & Tx Room 1 - G/F	46	0%	46	04-Jul-19	26-Aug-19	[Red bar from Jul 4 to Aug 26]			
ADB-EMGF1100	ABWF Works ready for E&M Mobilization to 11kV Swtich & Tx Room 2 - G/F	0	0%	0	04-Jul-19		◆			
ADB-EMGF1110	E&M Installation - 11kV Swtich & Tx Room 2 - G/F	46	0%	46	04-Jul-19	26-Aug-19	[Red bar from Jul 4 to Aug 26]			
ADB-EMGF1120	Cabling from NVB	12	0%	12	27-Aug-19	09-Sep-19			[Red bar from Aug 27 to Sep 9]	
ADB-EMGF1160	ABWF Works ready for E&M Mobilization to LV Switch Room - G/F	0	0%	0	04-Jul-19		◆			
ADB-EMGF1170	E&M Installation - LV Switch Room - G/F	34	0%	34	26-Jul-19	03-Sep-19			[Red bar from Jul 26 to Sep 3]	
ADB-EMGF1180	Cable laying - LV Switch Room - from G/F	24	0%	24	04-Sep-19	03-Oct-19			[Red bar from Sep 4 to Oct 3]	
ADB-EMGF1200	ABWF Works ready for E&M Mobilization to Generator Room & Fuel Tank Room - G/F	0	0%	0	04-Jul-19		◆			
ADB-EMGF1210	E&M Installation - Generator Room & Fuel Tank Room - G/F	70	0%	70	05-Sep-19	29-Nov-19			[Red bar from Sep 5 to Nov 29]	
ADB-EMGF1230	ABWF Works ready for E&M Mobilization to MVAC Plant Rooms - G/F	0	0%	0	04-Jul-19		◆			
ADB-EMGF1240	E&M Installation - MVAC Plant Rooms - G/F	76	0%	76	24-Aug-19	23-Nov-19			[Red bar from Aug 24 to Nov 23]	
ADB-EMGF1250	ABWF Works ready for E&M Mobilization to FS Plant Rooms - G/F	0	0%	0	04-Jul-19		◆			
ADB-EMGF1260	E&M Installation - FS Plant Rooms - G/F	60	0%	60	04-Jul-19	11-Sep-19			[Red bar from Jul 4 to Sep 11]	
ADB-EMGF1270	ABWF Works ready for E&M Mobilization to PD Plant Rooms - G/F	0	0%	0	04-Jul-19		◆			
ADB-EMGF1290	ABWF Works ready for E&M Mobilization to ELV Plant Rooms - G/F	0	0%	0	04-Jul-19		◆			
ADB-EMGF1300	E&M Installation - ELV Plant Rooms - G/F	50	0%	50	21-Aug-19	21-Oct-19			[Red bar from Aug 21 to Oct 21]	
1/F										
ADB-EM1F1000	ABWF Works ready for E&M Mobilization to General Areas - 1/F	0	0%	0	26-Jul-19			◆		
ADB-EM1F1010	E&M Installation - 1st fix - 1/F	40	0%	40	26-Jul-19	10-Sep-19			[Red bar from Jul 26 to Sep 10]	
ADB-EM1F1020	E&M Installation - 2nd fix - 1/F	40	0%	40	20-Aug-19	08-Oct-19			[Red bar from Aug 20 to Oct 8]	
ADB-EM1F1030	E&M Installation - Final fix - 1/F	40	0%	40	13-Sep-19	01-Nov-19			[Red bar from Sep 13 to Nov 1]	
ADB-EM1F1050	ABWF Works ready for E&M Mobilization to MVAC Plant Rooms - 1/F	0	0%	0	18-Jul-19			◆		
ADB-EM1F1060	E&M Installation - MVAC Plant Rooms - 1/F	64	0%	64	24-Aug-19	09-Nov-19			[Red bar from Aug 24 to Nov 9]	
ADB-EM1F1070	ABWF Works ready for E&M Mobilization to Electical Plant Rooms - 1/F	0	0%	0	18-Jul-19			◆		
ADB-EM1F1090	ABWF Works ready for E&M Mobilization to ELV Plant Rooms - 1/F	0	0%	0	18-Jul-19			◆		
ADB-EM1F1100	E&M Installation - ELV Plant Rooms - 1/F	52	0%	52	21-Aug-19	23-Oct-19			[Red bar from Aug 21 to Oct 23]	
Roof										
ADB-EMRF1000	ABWF Works ready for E&M Mobilization to General Areas - Roof	0	0%	0	30-Aug-19				◆	
ADB-EMRF1010	E&M Installation - 1st fix - Roof	25	0%	25	30-Aug-19	28-Sep-19			[Red bar from Aug 30 to Sep 28]	
ADB-EMRF1013	E&M Installation - 2nd fix - Roof	25	0%	25	19-Sep-19	19-Oct-19			[Red bar from Sep 19 to Oct 19]	
ADB-EMRF1020	ABWF Works ready for E&M Mobilization to Cooling Tower Area - Roof	0	0%	0	30-Aug-19				◆	
ADB-EMRF1030	E&M Installation - Cooling Tower Area - Roof	90	0%	90	30-Aug-19	16-Dec-19			[Red bar from Aug 30 to Dec 16]	
Lift Installation (L01)										
ADB-LF1010	Access to lift shaft and lift machine room	0	0%	0	30-Aug-19				◆	
ADB-LF1020	Lift & lift machine room installation	80	0%	80	30-Aug-19	04-Dec-19			[Red bar from Aug 30 to Dec 4]	
E&M Works for Maintenance Depot										
Installation										
G/F										
MD-EMGF1000	ABWF Works ready for E&M Mobilization to General Areas - G/F	0	0%	0	10-Jul-19			◆		
MD-EMGF1010	E&M Installation - 1st fix - G/F	40	0%	40	10-Jul-19	24-Aug-19			[Red bar from Jul 10 to Aug 24]	
MD-EMGF1020	E&M Installation - 2nd fix - G/F	40	0%	40	19-Aug-19	05-Oct-19			[Red bar from Aug 19 to Oct 5]	
MD-EMGF1040	ABWF Works ready for E&M Mobilization to LV Switch Room - G/F	0	0%	0	11-Jul-19			◆		
MD-EMGF1050	E&M Installation - LV Switch Room - G/F	90	0%	90	26-Jul-19	11-Nov-19			[Red bar from Jul 26 to Nov 11]	
MD-EMGF1080	ABWF Works ready for E&M Mobilization to Generator & Fuel Tank Rooms - G/F	0	0%	0	27-Jul-19			◆		
MD-EMGF1090	E&M Installation - Generator & Fuel Tank Rooms - G/F	75	0%	75	05-Sep-19	05-Dec-19			[Red bar from Sep 5 to Dec 5]	
MD-EMGF1110	ABWF Works ready for E&M Mobilization to Electrical Plant Rooms - G/F	0	0%	0	27-Jul-19			◆		
MD-EMGF1120	E&M Installation - Electrical Plant Rooms - G/F	70	0%	70	21-Aug-19	13-Nov-19			[Red bar from Aug 21 to Nov 13]	

**CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019**

P 14/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
MD-EMGF1130	ABWF Works ready for E&M Mobilization to MVAC Plant Rooms - G/F	0	0%	0	27-Jul-19					
MD-EMGF1140	E&M Installation - MVAC Plant Rooms - G/F	90	0%	90	27-Jul-19					
MD-EMGF1150	ABWF Works ready for E&M Mobilization to FS Plant Rooms - G/F	0	0%	0	27-Jul-19					
MD-EMGF1160	E&M Installation - FS Plant Rooms - G/F	90	0%	90	27-Jul-19					
MD-EMGF1170	ABWF Works ready for E&M Mobilization to PD Plant Rooms - G/F	0	0%	0	27-Jul-19					
MD-EMGF1180	E&M Installation - PD Plant Rooms - G/F	85	0%	85	27-Jul-19					
MD-EMGF1190	ABWF Works ready for E&M Mobilization to Elv Plant Rooms - G/F	0	0%	0	27-Jul-19					
MD-EMGF1200	E&M Installation - Elv Plant Rooms - G/F	60	0%	60	17-Aug-19					
R/F										
MD-EMRF1000	ABWF Works ready for E&M Mobilization to R/F	0	0%	0	29-Aug-19					
MD-EMRF1010	E&M Installation - 1st fix - R/F	30	0%	30	29-Aug-19					
E&M Works for North Ventilation Building										
Installation										
TVF Installation										
SB-NVB-TVF3										
TVF-NVB0220	Preparation Works	6	0%	6	20-Jun-19	26-Jun-19				
TVF-NVB1480	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	27-Jun-19	11-Jul-19				
TVF-NVB1490	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	12-Jul-19	25-Jul-19				
TVF-NVB1500	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	26-Jul-19	01-Aug-19				
TVF-NVB1510	Leakage test for TVF	8	0%	8	02-Aug-19	10-Aug-19				
SB-NVB-TVF4										
TVF-NVB0230	Preparation Works	6	0%	6	20-Jun-19	26-Jun-19				
TVF-NVB1520	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	27-Jun-19	11-Jul-19				
TVF-NVB1530	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	12-Jul-19	25-Jul-19				
TVF-NVB1540	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	26-Jul-19	01-Aug-19				
TVF-NVB1550	Leakage test for TVF	8	0%	8	02-Aug-19	10-Aug-19				
NB-NVB-TVF2										
TVF-NVB0110	Preparation Works	6	0%	6	12-Jul-19	18-Jul-19				
TVF-NVB1040	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	19-Jul-19	01-Aug-19				
TVF-NVB1050	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	02-Aug-19	15-Aug-19				
TVF-NVB1060	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	16-Aug-19	22-Aug-19				
TVF-NVB1070	Leakage test for TVF	8	0%	8	23-Aug-19	31-Aug-19				
NB-NVB-TVF3										
TVF-NVB0120	Preparation Works	6	0%	6	12-Jul-19	18-Jul-19				
TVF-NVB1080	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	19-Jul-19	01-Aug-19				
TVF-NVB1090	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	02-Aug-19	15-Aug-19				
TVF-NVB1100	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	16-Aug-19	22-Aug-19				
TVF-NVB1110	Leakage test for TVF	8	0%	8	23-Aug-19	31-Aug-19				
SB-NVB-TVF1										
TVF-NVB0200	Preparation Works	6	0%	6	02-Aug-19	08-Aug-19				
TVF-NVB1400	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	09-Aug-19	22-Aug-19				
TVF-NVB1410	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	23-Aug-19	05-Sep-19				
TVF-NVB1420	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	06-Sep-19	12-Sep-19				
TVF-NVB1430	Leakage test for TVF	8	0%	8	13-Sep-19	23-Sep-19				
SB-NVB-TVF2										
TVF-NVB0210	Preparation Works	6	0%	6	02-Aug-19	08-Aug-19				
TVF-NVB1440	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	09-Aug-19	22-Aug-19				
TVF-NVB1450	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	23-Aug-19	05-Sep-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 15/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
TVF-NVB1460	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	06-Sep-19	12-Sep-19					
TVF-NVB1470	Leakage test for TVF	8	0%	8	13-Sep-19	23-Sep-19					
NB-NVB-TVF-1											
TVF-NVB0100	Preparation Works	6	0%	6	23-Aug-19	29-Aug-19					
TVF-NVB1000	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	30-Aug-19	12-Sep-19					
TVF-NVB1010	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	13-Sep-19	27-Sep-19					
NB-NVB-TVF-4											
TVF-NVB0130	Preparation Works	6	0%	6	23-Aug-19	29-Aug-19					
TVF-NVB1120	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	30-Aug-19	12-Sep-19					
TVF-NVB1130	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	13-Sep-19	27-Sep-19					
NB-NVB-TVF-5											
TVF-NVB0140	Preparation Works	6	0%	6	12-Jul-19	18-Jul-19					
TVF-NVB1160	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	19-Jul-19	01-Aug-19					
TVF-NVB1170	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	02-Aug-19	15-Aug-19					
TVF-NVB1180	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	16-Aug-19	22-Aug-19					
TVF-NVB1190	Leakage test for TVF	8	0%	8	23-Aug-19	31-Aug-19					
NB-NVB-TVF-6											
TVF-NVB0150	Preparation Works	6	0%	6	12-Jul-19	18-Jul-19					
TVF-NVB1200	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	19-Jul-19	01-Aug-19					
TVF-NVB1210	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	02-Aug-19	15-Aug-19					
TVF-NVB1220	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	16-Aug-19	22-Aug-19					
TVF-NVB1230	Leakage test for TVF	8	0%	8	23-Aug-19	31-Aug-19					
NB-NVB-TVF-7											
TVF-NVB0160	Preparation Works	6	0%	6	02-Aug-19	08-Aug-19					
TVF-NVB1240	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	09-Aug-19	22-Aug-19					
TVF-NVB1250	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	23-Aug-19	05-Sep-19					
TVF-NVB1260	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	06-Sep-19	12-Sep-19					
TVF-NVB1270	Leakage test for TVF	8	0%	8	13-Sep-19	23-Sep-19					
NB-NVB-TVF-8											
TVF-NVB0170	Preparation Works	6	0%	6	02-Aug-19	08-Aug-19					
TVF-NVB1280	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	09-Aug-19	22-Aug-19					
TVF-NVB1290	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	23-Aug-19	05-Sep-19					
TVF-NVB1300	Ventilation fan and duct installation - Fan Room (G/F)	6	0%	6	06-Sep-19	12-Sep-19					
TVF-NVB1310	Leakage test for TVF	8	0%	8	13-Sep-19	23-Sep-19					
NB-NVB-TVF-9											
TVF-NVB0180	Preparation Works	6	0%	6	23-Aug-19	29-Aug-19					
TVF-NVB1320	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	30-Aug-19	12-Sep-19					
TVF-NVB1330	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	13-Sep-19	27-Sep-19					
NB-NVB-TVF-10											
TVF-NVB0190	Preparation Works	6	0%	6	23-Aug-19	29-Aug-19					
TVF-NVB1360	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	12	0%	12	30-Aug-19	12-Sep-19					
TVF-NVB1370	Damper/Silencer and duct installation - Lower Attenuator Room (B1/F)	12	0%	12	13-Sep-19	27-Sep-19					
B2/F											
NVB-EMB21010	E&M Installation - 1st fix - B2/F	50	82%	9	21-Nov-18 A	29-Jun-19					
NVB-EMB21020	E&M Installation - 2nd fix - B2/F	50	56%	22	28-Nov-18 A	26-Jul-19					
NVB-EMB21030	E&M Installation - Final fix - B2/F	50	5%	48	24-Jan-19 A	21-Sep-19					
NVB-EMB21060	E&M Installation - Electrical Plant Rooms - B2/F	90	0%	90	20-Jun-19	05-Oct-19					
NVB-EMB21080	E&M Installation - MVAC Plant Rooms - B2/F	60	0%	60	20-Jun-19	29-Aug-19					

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 16/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
NVB-EMB21100	E&M Installation - FS Plant Rooms - B2/F	45	0%	45	20-Jun-19	12-Aug-19				
NVB-EMB21120	E&M Installation - PD Plant Rooms - B2/F	60	0%	60	08-Jul-19	16-Sep-19				
NVB-EMB21140	E&M Installation - Elv Plant Rooms - B2/F	45	0%	45	16-Aug-19	11-Oct-19				
B1/F										
NVB-EMB11010	E&M Installation - 1st fix - B1/F	50	73%	14	19-Nov-18 A	06-Jul-19				
NVB-EMB11020	E&M Installation - 2nd fix - B1/F	50	55%	23	26-Nov-18 A	01-Aug-19				
NVB-EMB11030	E&M Installation - Final fix - B1/F	50	4%	48	24-Jan-19 A	27-Sep-19				
NVB-EMB11060	E&M Installation - Electrical Plant Rooms - B1/F	90	0%	90	20-Jun-19	05-Oct-19				
NVB-EMB11080	E&M Installation - MVAC Plant Rooms - B1/F	60	0%	60	20-Jun-19	29-Aug-19				
NVB-EMB11100	E&M Installation - Elv Plant Rooms - B1/F	45	0%	45	16-Aug-19	11-Oct-19				
G/F										
NVB-EMGF1010	E&M Installation - 1st fix - G/F	50	83%	9	01-Aug-18 A	29-Jun-19				
NVB-EMGF1020	E&M Installation - 2nd fix - G/F	50	56%	22	08-Aug-18 A	26-Jul-19				
NVB-EMGF1030	E&M Installation - Final fix - G/F	50	4%	48	24-Jan-19 A	21-Sep-19				
NVB-EMGF1070	Installation by CLP - CLPP HV Switch Room - G/F	82	51.22%	40	14-Feb-19 A	06-Aug-19				
NVB-EMGF1120	E&M Installation - Genset Room & Fuel Tank Room - G/F	80	0%	80	05-Sep-19	11-Dec-19				
NVB-EMGF1140	E&M Installation - Electrical Plant Rooms - G/F	50	0%	50	24-Aug-19	25-Oct-19				
NVB-EMGF1160	E&M Installation - MVAC Plant Rooms - G/F	52	0%	52	19-Aug-19	21-Oct-19				
NVB-EMGF1180	E&M Installation - FS Plant Rooms - G/F	90	0%	90	20-Jun-19	05-Oct-19				
NVB-EMGF1200	E&M Installation - PD Plant Rooms - G/F	90	0%	90	08-Jul-19	24-Oct-19				
1/F										
NVB-EM1F1010	E&M Installation - 1st fix - 1/F	50	65%	18	03-Sep-18 A	11-Jul-19				
NVB-EM1F1020	E&M Installation - 2nd fix - 1/F	50	49%	26	10-Sep-18 A	09-Aug-19				
NVB-EM1F1030	E&M Installation - Final fix - 1/F	50	5%	48	31-Jan-19 A	08-Oct-19				
NVB-EM1F1050	E&M Installation - LV Switch Room - 1/F	40	0%	40	26-Jul-19	10-Sep-19				
NVB-EM1F1060	Cable laying - LV Switch Room - 1/F	58	0%	58	30-Aug-19	08-Nov-19				
NVB-EM1F1090	E&M Installation - 11kV Switch & Tx Room 1 - 1/F	60	0%	60	02-Jul-19	10-Sep-19				
NVB-EM1F1150	E&M Installation - 11kV Switch & Tx Room 2 - 1/F	60	0%	60	02-Jul-19	10-Sep-19				
NVB-EM1F1220	E&M Installation - Electrical Plant Rooms - 1/F	50	0%	50	21-Aug-19	21-Oct-19				
NVB-EM1F1240	E&M Installation - MVAC Plant Rooms - 1/F	90	0%	90	20-Jun-19	05-Oct-19				
NVB-EM1F1260	E&M Installation - FS Plant Rooms - 1/F	90	0%	90	19-Jul-19	04-Nov-19				
2/F										
NVB-EM2F1010	E&M Installation - 1st fix - 2/F	50	63%	19	08-Oct-18 A	12-Jul-19				
NVB-EM2F1020	E&M Installation - 2nd fix - 2/F	50	40%	30	15-Oct-18 A	16-Aug-19				
NVB-EM2F1030	E&M Installation - Final fix - 2/F	50	5%	48	07-Feb-19 A	14-Oct-19				
NVB-EM2F1060	E&M Installation - Electrical Plant Rooms - 2/F	50	0%	50	21-Aug-19	21-Oct-19				
NVB-EM2F1080	E&M Installation - MVAC Plant Rooms - 2/F	60	0%	60	19-Aug-19	30-Oct-19				
NVB-EM2F1100	E&M Installation - Elv Plant Rooms - 2/F	45	0%	45	21-Aug-19	15-Oct-19				
Lift Installation (L01 & L02)										
NVB-LF1020	Lift & lift machine room installation	73	0%	73	19-Jul-19	15-Oct-19				
Remaining E&M Works for Kiosk N2 (Structure Completed under KD2)										
EN2120	ABWF Works (Door, windows, tiles)	30	0%	30	20-Jun-19	25-Jul-19				
EN2130	E&M Works	31	0%	31	26-Jul-19	30-Aug-19				
EN2140	Testing & Commissioning	12	0%	12	31-Aug-19	13-Sep-19				
Key Date 3 - Satellite Control Building & TCSS Provision										
Building Structure										
SCB140	First Floor	12	25%	9	14-May-19 A	29-Jun-19				
SCB150	Lower Roof Slab	12	0%	12	02-Jul-19	15-Jul-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 17/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
SCB160	Second Floor	12	0%	12	16-Jul-19	29-Jul-19					
SCB170	Upper Roof Slab	15	0%	15	30-Jul-19	15-Aug-19					
ABWF Works (for All)											
ASCB1000	Blockwork Walls	19	0%	19	16-Jul-19	06-Aug-19					
ASCB1010	Door and Window Frames	19	0%	19	16-Jul-19	06-Aug-19					
ASCB1020	ABWF Works to Plant Rooms G/F	60	0%	60	23-Jul-19	02-Oct-19					
ASCB1021	ABWF Works to Plant Rooms 1/F	60	0%	60	30-Jul-19	10-Oct-19					
ASCB1022	ABWF Works to Plant Rooms 2/F	60	0%	60	06-Aug-19	17-Oct-19					
ASCB1030	ABWF Works to Office and Corridors G/F	95	0%	95	23-Jul-19	13-Nov-19					
ASCB1031	ABWF Works to Office and Corridors 1/F	95	0%	95	06-Aug-19	27-Nov-19					
ASCB1040	ABWF Works to Toilets 1/F	103	0%	103	23-Jul-19	22-Nov-19					
ASCB1050	Waterproofing and Roofing	50	0%	50	23-Jul-19	19-Sep-19					
ASCB1060	External Cladding and Wall Plastering	101	0%	101	23-Jul-19	20-Nov-19					
Provision for TCSS Installation											
SCB210	Cable Containment Installation to enable TCSS installation	62	0%	62	04-Sep-19	18-Nov-19					
Key Date 5 - E&M Works for TCB, Toll Area, Kiosk N1, Underpass, Plant Rm, and Approach Roads											
Carpark Canopy											
ETCB150	Steelwork for Canopy Structure	90	0%	90	20-Jun-19	05-Oct-19					
E&M Works for TCB											
Installation											
Basement											
TCB-EM1001	E&M Installation - 1st fix - Basement	60	18%	49	10-Apr-19 A	17-Aug-19					
TCB-EM1002	E&M Installation - 2nd fix - Basement	60	1%	59	04-Jun-19 A	29-Oct-19					
G/F											
TCB-EMGF1010	E&M Installation - 1st fix - G/F	60	51%	29	15-Feb-19 A	25-Jul-19					
TCB-EMGF1020	E&M Installation - 2nd fix - G/F	60	1%	59	15-May-19 A	04-Oct-19					
TCB-EMGF1070	Installation by CLP - CLP Tx Room - G/F	60	70%	18	14-Feb-19 A	11-Jul-19					
TCB-EMGF1100	ABWF Works ready for E&M Mobilization to LV Switch Room - G/F	0	100%	0	20-Jun-19 A						
TCB-EMGF1110	E&M Installation - LV Switch Room - G/F	70	0%	70	26-Jul-19	18-Oct-19					
TCB-EMGF1140	ABWF Works ready for E&M Mobilization to Generator & Fuel Tank Rooms - G/F	0	0%	0	20-Jun-19						
TCB-EMGF1150	E&M Installation - Generator & Fuel Tank Rooms - G/F	90	0%	90	05-Sep-19	23-Dec-19					
TCB-EMGF1170	ABWF Works ready for E&M Mobilization to Electrical Plant Rooms - G/F	0	0%	0	20-Jun-19						
TCB-EMGF1190	ABWF Works ready for E&M Mobilization to MVAC Plant Rooms - G/F	0	0%	0	20-Jun-19						
TCB-EMGF1200	E&M Installation - MVAC Plant Rooms - G/F	90	0%	90	16-Jul-19	31-Oct-19					
TCB-EMGF1210	ABWF Works ready for E&M Mobilization to FS Plant Rooms - G/F	0	0%	0	20-Jun-19						
TCB-EMGF1220	E&M Installation - FS Plant Rooms - G/F	90	0%	90	29-Jun-19	16-Oct-19					
TCB-EMGF1230	ABWF Works ready for E&M Mobilization to PD Plant Rooms - G/F	0	0%	0	20-Jun-19						
TCB-EMGF1240	E&M Installation - PD Plant Rooms - G/F	60	0%	60	08-Jul-19	16-Sep-19					
1/F											
TCB-EM1F1010	E&M Installation - 1st fix - 1/F	60	61%	23	26-Mar-19 A	18-Jul-19					
TCB-EM1F1020	E&M Installation - 2nd fix - 1/F	60	1%	59	20-May-19 A	27-Sep-19					
TCB-EM1F1050	ABWF Works ready for E&M Mobilization to Electrical Plant Rooms - 1/F	0	0%	0	20-Jun-19						
TCB-EM1F1060	E&M Installation - Electrical Plant Rooms - 1/F	90	0%	90	24-Aug-19	11-Dec-19					
TCB-EM1F1070	ABWF Works ready for E&M Mobilization to FS Plant Rooms - 1/F	0	0%	0	20-Jun-19						
TCB-EM1F1080	E&M Installation - FS Plant Rooms - 1/F	90	0%	90	29-Jun-19	16-Oct-19					
TCB-EM1F1090	ABWF Works ready for E&M Mobilization to PD Plant Rooms - 1/F	0	0%	0	20-Jun-19						
2/F											
TCB-EM2F1010	E&M Installation - 1st fix - 2/F	48	65%	17	04-Apr-19 A	10-Jul-19					

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 18/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
TCB-EM2F1020	E&M Installation - 2nd fix - 2/F	48	1%	48	30-May-19 A	04-Sep-19					
TCB-EM2F1050	ABWF Works ready for E&M Mobilization to Electrical Plant Rooms - 2/F	0	0%	0	19-Jul-19						
TCB-EM2F1070	ABWF Works ready for E&M Mobilization to MVAC Plant Rooms - 2/F	0	0%	0	19-Jul-19						
TCB-EM2F1080	E&M Installation - MVAC Plant Rooms - 2/F	90	0%	90	19-Jul-19	04-Nov-19					
TCB-EM2F1090	ABWF Works ready for E&M Mobilization to Elv Plant Rooms - 2/F	0	0%	0	19-Jul-19						
TCB-EM2F1100	E&M Installation - Elv Plant Rooms - 2/F	60	0%	60	17-Aug-19	29-Oct-19					
Roof											
TCB-EMRF1000	ABWF Works ready for E&M Mobilization to Roof	0	0%	0	19-Jul-19						
TCB-EMRF1010	E&M Installation - 1st fix - Roof	50	0%	50	19-Jul-19	16-Sep-19					
TCB-EMRF1020	E&M Installation - 2nd fix - Roof	50	0%	50	19-Sep-19	18-Nov-19					
Lift Installation (L01)											
TCB-LF1000	Access to lift shaft and lift machine room	0	0%	0	24-Jun-19						
TCB-LF1010	Lift & lift machine room installation	90	0%	90	19-Jul-19	04-Nov-19					
Toll Area											
South Bound											
ETA120	Possess Portions IX, XIX, XX1a, XX1b	0	0%	0	20-Jun-19						
ETA130	Installation of South Bound Toll Booths	30	0%	30	20-Jun-19	25-Jul-19					
ETA140	South Bound Toll Booths - E&M installation 1st fix	36	0%	36	26-Jul-19	05-Sep-19					
ETA150	Toll Booth Subway - E&M installation 1st fix	48	0%	48	06-Sep-19	04-Nov-19					
North Bound											
ETA190	Possess Portion XI	0	0%	0	20-Jun-19						
ETA200	Installation of North Bound Toll Booths	30	0%	30	20-Jun-19	25-Jul-19					
ETA210	North Bound Toll Booths - E&M installation 1st fix	36	0%	36	26-Jul-19	05-Sep-19					
ETA220	Toll Booth Subway - E&M installation 1st fix	48	0%	48	06-Sep-19	04-Nov-19					
Kiosk N1											
EN120	Possess Portion IX	0	0%	0	20-Jun-19						
EN130	Structure	48	0%	48	20-Jun-19	15-Aug-19					
EN140	ABWF Works (Door, windows, tiles)	30	0%	30	16-Aug-19	20-Sep-19					
Underpass											
E&M Works at Underpass											
EU110	Satge 1 E&M Works Completed for TCSS (under KD4)	0	0%	0		04-Jul-19					
VU110	Jet Fans installation	24	0%	24	04-Jul-19	31-Jul-19					
VU140	Dampers installation	24	0%	24	01-Aug-19	28-Aug-19					
VU150	Cabling Works	36	0%	36	04-Jul-19	15-Aug-19					
VU170	High Level works - Tunnel Lighting	39	0%	39	15-Aug-19	02-Oct-19					
VU180	Cladding Works	25	0%	25	15-Aug-19	13-Sep-19					
Plant Room											
E&M Works											
EPR120	Blockwork Wall & ABWF Works	90	60%	36	02-Nov-18 A	01-Aug-19					
EPR130	E&M Installation	90	15%	77	03-Jan-19 A	10-Oct-19					
EPR140	External Works	82	0%	82	15-Aug-19	22-Nov-19					
VU160	Pressurization Fans Installation	24	0%	24	01-Aug-19	28-Aug-19					
Deck Void											
TD1, TD2, RB_W											
DV180	Possess Portions X, IX and XI	0	0%	0	20-Jun-19						
Bridge H1, G1, G2											
DV110	Possess Portions IX	0	0%	0	20-Jun-19						
DV120	Electrical Installation - Bridge H1	28	0%	28	20-Jun-19	23-Jul-19					

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 19/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
DV130	Electrical Installation - Bridge G1	28	0%	28	24-Jul-19	24-Aug-19				
DV140	Electrical Installation - Bridge G2	28	0%	28	26-Aug-19	27-Sep-19				
Approach Roads										
Under Portions IX, XI, XX										
AR120	Possess Portions IX and XI	0	0%	0	20-Jun-19					
AR130	Cabling works - Portion IX	45	0%	45	20-Jun-19	12-Aug-19				
AR133	Cabling works - Portion XI	45	0%	45	13-Aug-19	05-Oct-19				
AR140	Road lighting installation & termination - Portion IX	25	0%	25	19-Jul-19	16-Aug-19				
AR145	Road lighting installation & termination - Portion XI	25	0%	25	10-Sep-19	11-Oct-19				
Under Portion X										
AR170	Possess Portions X	0	0%	0	20-Jun-19					
AR176	Underground Cable Duct Installation (by others)	61	50%	31	22-Apr-19 A	26-Jul-19				
AR180	Cabling works in portion X	90	0%	90	26-Jul-19	12-Nov-19				
AR190	Road lighting installation & termination in portion X	90	0%	90	09-Aug-19	26-Nov-19				
Key Date 6B - E&M Works for South Vent Duct, Tunnel, and Approach Roads										
E&M Works										
SVD120	Access to Portions III	0	0%	0	17-Jul-19					
Service Gallery										
Ch 7200 - 5000										
TNL-SG1000	Drilling works CH7200 - 5000	12	14%	10	16-Apr-19 A	03-Jul-19				
TNL-SG1010	Wall Mounted Pipe Module Installation CH7200 - 5000	30	14%	26	23-Apr-19 A	02-Aug-19				
TNL-SG1020	Ceiling Mounted Module Delivery CH7200 - 5000	30	14%	26	30-Apr-19 A	31-Aug-19				
TNL-SG1030	High Level 2nd Fix and Final Fix Installation CH7200 - 5000	46	0%	46	03-Sep-19	30-Oct-19				
TNL-SG1040	Cabling Works CH7200 - 5000	29	0%	29	31-Aug-19	08-Oct-19				
CH5000 - 3050										
TNL-SG1060	Drilling works CH5000 - 3050	12	0%	12	17-Jul-19	30-Jul-19				
TNL-SG1070	Wall Mounted Pipe Module Installation CH5000 - 3050	30	0%	30	02-Aug-19	06-Sep-19				
TNL-SG1080	Ceiling Mounted Module Delivery CH5000 - 3050	30	0%	30	06-Sep-19	15-Oct-19				
Road Level & OHVD										
Ch 7200 - 5000										
Ch 7200 - 6700										
TNU-RL1770	Bracket fixing on side wall - CH7200 to 6700	8	83.01%	1	15-Apr-19 A	21-Jun-19				
TNU-RL1775	Installation Works by Others (to be coordinated)	50	0%	50	21-Jun-19	19-Aug-19				
TNU-RL1790	Lighting in the middle of tunnels - CH7200 to 6700	8	0%	8	20-Jun-19	28-Jun-19				
TNU-RL1800	FH/ HR pipe installation - CH7200 to 6700	8	70%	2	02-Apr-19 A	03-Jul-19				
TNU-RL1830	Cabling Works on Brackets - CH7200 to 6700	14	38.99%	9	16-Apr-19 A	12-Jul-19				
TNU-RL1840	MSFD delivery in OHVD - CH7200 to 6700	9	43%	5	10-Jun-19 A	09-Jul-19				
TNU-RL1870	MSFD installation works in OHVD - CH7200 to 6700	9	43%	5	10-Jun-19 A	15-Jul-19				
TNU-RL1880	High level wiring works and remaining High level works in the middle of tunnels - CH7200 to 6700	20	0%	20	12-Jul-19	05-Aug-19				
TNU-RL1910	Low level works - FS nicle module - CH7200 to 6700	10	0%	10	24-Jul-19	05-Aug-19				
TNU-RL1930	Low level works - FS nicle connection - CH7200 to 6700	10	0%	10	26-Jul-19	07-Aug-19				
TNU-RL1940	Final connection to small powers - CH7200 to 6700	10	0%	10	07-Aug-19	19-Aug-19				
TNU-RL1970	Cladding works - CH7200 to 6700	13	0%	13	19-Aug-19	03-Sep-19				
Ch 6700 - 6100										
TNU-RL1000	Bracket fixing on side wall - CH6700 to 6100	10	83%	2	15-Apr-19 A	24-Jun-19				
TNU-RL1005	Installation Works by Others (to be coordinated)	72	0%	72	24-Jun-19	17-Sep-19				
TNU-RL1010	Lighting in the middle of tunnels - CH6700 to 6100	9	13%	8	11-Jun-19 A	09-Jul-19				
TNU-RL1020	FH/ HR pipe installation - CH6700 to 6100	10	85%	2	16-Apr-19 A	11-Jul-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 20/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
TNU-RL1030	Cabling Works on Brackets - CH6700 to 6100	17	15%	14	16-Apr-19 A	30-Jul-19				
TNU-RL1040	MSFD delivery in OHVD - CH6700 to 6100	11	44.01%	6	18-May-19 A	16-Jul-19				
TNU-RL1050	MSFD installation works in OHVD - CH6700 to 6100	11	44.01%	6	18-May-19 A	23-Jul-19				
TNU-RL1060	High level wiring works and remaining High level works in the middle of tunnels - CH6700 to 6100	24	0%	24	05-Aug-19	02-Sep-19				
TNU-RL1070	Low level works - FS nicle module - CH6700 to 6100	12	0%	12	19-Aug-19	02-Sep-19				
TNU-RL1080	Low level works - FS nicle connection - CH6700 to 6100	12	0%	12	21-Aug-19	04-Sep-19				
TNU-RL1090	Final connection to small powers - CH6700 to 6100	10	0%	10	04-Sep-19	17-Sep-19				
TNU-RL1100	Cladding works - CH6700 to 6100	15	0%	15	17-Sep-19	05-Oct-19				
Ch6100 - 5600										
TNU-RL1110	Bracket fixing on side wall - CH6100 to 5600	8	83.01%	1	15-Apr-19 A	25-Jun-19				
TNU-RL1115	Installation Works by Others (to be coordinated)	91	0%	91	25-Jun-19	12-Oct-19				
TNU-RL1120	Lighting in the middle of tunnels - CH6100 to 5600	8	95%	0	11-Jun-19 A	10-Jul-19				
TNU-RL1130	FH/ HR pipe installation - CH6100 to 5600	8	90%	1	09-Apr-19 A	12-Jul-19				
TNU-RL1140	Cabling Works on Brackets - CH6100 to 5600	14	37%	9	23-Apr-19 A	09-Aug-19				
TNU-RL1150	MSFD delivery in OHVD - CH6100 to 5600	9	0%	9	16-Jul-19	26-Jul-19				
TNU-RL1160	MSFD installation works in OHVD - CH6100 to 5600	9	0%	9	26-Jul-19	06-Aug-19				
TNU-RL1170	High level wiring works and remaining High level works in the middle of tunnels - CH6100 to 5600	20	0%	20	02-Sep-19	26-Sep-19				
TNU-RL1180	Low level works - FS nicle module - CH6100 to 5600	10	0%	10	13-Sep-19	26-Sep-19				
TNU-RL1190	Low level works - FS nicle connection - CH6100 to 5600	10	0%	10	17-Sep-19	28-Sep-19				
CH 5600 - 5000										
TNU-RL1220	Bracket fixing on side wall - CH5600 to 5000	10	83%	2	15-Apr-19 A	27-Jun-19				
TNU-RL1225	Installation Works by Others (to be coordinated)	113	0%	113	27-Jun-19	09-Nov-19				
TNU-RL1240	FH/ HR pipe installation - CH5600 to 5000	10	85%	2	16-Apr-19 A	10-Sep-19				
TNU-RL1250	Cabling Works on Brackets - CH5600 to 5000	17	44%	10	23-Apr-19 A	23-Sep-19				
TNU-RL1260	MSFD delivery in OHVD - CH5600 to 5000	11	0%	11	26-Jul-19	08-Aug-19				
TNU-RL1270	MSFD installation works in OHVD - CH5600 to 5000	11	0%	11	08-Aug-19	21-Aug-19				
CH5000 - 3050										
CH5000 - 4500										
TNU-RL1780	Bracket fixing on side wall - CH5000 to 4500	8	15%	7	15-Jun-19 A	24-Jul-19				
TNU-RL1785	Installation Works by Others (to be coordinated)	110	0%	110	24-Jul-19	03-Dec-19				
TNU-RL1810	Lighting in the middle of tunnels - CH5000 to 4500	8	0%	8	18-Sep-19	26-Sep-19				
TNU-RL1820	FH/ HR pipe installation - CH5000 to 4500	8	75%	2	06-May-19 A	28-Sep-19				
TNU-RL1850	Cabling Works on Brackets - CH5000 to 4500	14	22%	11	14-May-19 A	14-Oct-19				
CH4500 - 4000										
TNU-RL1330	Bracket fixing on side wall - CH4500 to 4000	8	0%	8	24-Jul-19	02-Aug-19				
TNU-RL1335	Installation Works by Others (to be coordinated)	122	0%	122	02-Aug-19	28-Dec-19				
TNU-RL1350	FH/ HR pipe installation - CH4500 to 4000	8	65%	3	14-May-19 A	11-Oct-19				
TNU-RL1360	Cabling Works on Brackets - CH4500 to 4000	14	22%	11	20-May-19 A	26-Oct-19				
CH4000 - 3500										
TNU-RL1440	Bracket fixing on side wall - CH4000 to 3500	8	0%	8	02-Aug-19	12-Aug-19				
TNU-RL1445	Installation Works by Others (to be coordinated)	134	0%	134	12-Aug-19	22-Jan-20				
TNU-RL1460	FH/ HR pipe installation - CH4000 to 3500	8	35%	5	14-May-19 A	24-Oct-19				
CH3500 - 3050										
TNU-RL1550	Bracket fixing on side wall - CH3500 to 3050	8	0%	8	12-Aug-19	21-Aug-19				
TNU-RL1555	Installation Works by Others (to be coordinated)	146	0%	146	21-Aug-19	18-Feb-20				
Key Date 7 - E&M Works for Satellite Control Building and Kiosks S1&S2										
E&M Works for Satellite Control Building										
E&M Works										

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 21/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
Installation											
GF											
SCB-EMGF10	ABWF Works ready for E&M Mobilization to General Areas - G/F	0	0%	0	03-Sep-19						
SCB-EMGF10	E&M Installation - 1st fix - G/F	30	0%	30	03-Sep-19						
SCB-EMGF10	ABWF Works ready for E&M Mobilization to Generator Room & Fuel Tank Room - G/F	0	0%	0	03-Sep-19						
SCB-EMGF10	ABWF Works ready for E&M Mobilization to LV Switch Room - G/F	0	0%	0	28-Aug-19						
SCB-EMGF10	E&M Installation - LV Switch Room - G/F	60	0%	60	02-Sep-19						
SCB-EMGF11	ABWF Works ready for E&M Mobilization to CLP Tx Room - G/F	0	0%	0	06-Aug-19						
SCB-EMGF11	E&M Installation - CLP Tx Room - G/F	18	0%	18	27-Aug-19						
SCB-EMGF11	Inspection & Handover to CLP	6	0%	6	18-Sep-19						
SCB-EMGF11	ABWF Works ready for E&M Mobilization to FS Plant Rooms - G/F	0	0%	0	03-Sep-19						
SCB-EMGF11	E&M Installation - FS Plant Rooms - G/F	80	0%	80	17-Sep-19						
SCB-EMGF11	ABWF Works ready for E&M Mobilization to PD Plant Rooms - G/F	0	0%	0	03-Sep-19						
SCB-EMGF12	E&M Installation - PD Plant Rooms - G/F	90	0%	90	03-Sep-19						
1F											
SCB-EM1F10	ABWF Works ready for E&M Mobilization to General Areas - 1/F	0	0%	0	18-Sep-19						
SCB-EM1F10	E&M Installation - 1st fix - 1/F	30	0%	30	18-Sep-19						
SCB-EM1F10	ABWF Works ready for E&M Mobilization to Computer Room (TCSS) - 1/F	0	0%	0	10-Sep-19						
SCB-EM1F10	ABWF Works ready for E&M Mobilization to EL Room - 1/F	0	0%	0	10-Sep-19						
SCB-EM1F10	ABWF Works ready for E&M Mobilization to FS Plant Rooms - 1/F	0	0%	0	10-Sep-19						
SCB-EM1F11	E&M Installation - FS Plant Rooms - 1/F	85	0%	85	10-Sep-19						
SCB-EM1F11	ABWF Works ready for E&M Mobilization to Elv Plant Room - 1/F	0	0%	0	10-Sep-19						
Kiosk S2											
S2110	Possess Portion Vib	0	0%	0		01-Sep-19					
S2120	Structure	30	0%	30	02-Sep-19	09-Oct-19					
Key Date 6C - E&M Works for South Ventilation Building											
SVB-SEM1000	SEM Drawings ready for Structural Works for SVB	0	0%	0	06-Jul-19						
Installation											
TVF Installation											
NB-SVB-TVF-1											
SVB-TVF2000	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	30-Aug-19	05-Sep-19					
SVB-TVF2010	Damper/Silencer and duct installation - Lower Attenuator Room(B1/F)	7	0%	7	06-Sep-19	13-Sep-19					
NB-SVB-TVF-2											
SVB-TVF2040	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	06-Sep-19	12-Sep-19					
SVB-TVF2050	Damper/Silencer and duct installation - Lower Attenuator Room(B1/F)	7	0%	7	16-Sep-19	23-Sep-19					
NB-SVB-TVF-3											
SVB-TVF2080	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	13-Sep-19	20-Sep-19					
SB-SVB-TVF-1											
SVB-TVF2160	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	30-Aug-19	05-Sep-19					
SVB-TVF2170	Damper/Silencer and duct installation - Lower Attenuator Room(B1/F)	7	0%	7	06-Sep-19	13-Sep-19					
SB-SVB-TVF-2											
SVB-TVF2200	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	06-Sep-19	12-Sep-19					
SVB-TVF2210	Damper/Silencer and duct installation - Lower Attenuator Room(B1/F)	7	0%	7	16-Sep-19	23-Sep-19					
SB-SVB-TVF-3											
SVB-TVF2240	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	13-Sep-19	20-Sep-19					
SB-SVB-TVF-5											
SVB-TVF2320	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	30-Aug-19	05-Sep-19					
SVB-TVF2330	Damper/Silencer and duct installation - Lower Attenuator Room(B1/F)	7	0%	7	06-Sep-19	13-Sep-19					

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 22/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
SB-SVB-TVF-6											
SVB-TVF2360	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	06-Sep-19	12-Sep-19					
SVB-TVF2370	Damper/Silencer and duct installation - Lower Attenuator Room(B1/F)	7	0%	7	16-Sep-19	23-Sep-19					
SB-SVB-TVF-7											
SVB-TVF2400	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	30-Aug-19	05-Sep-19					
SVB-TVF2410	Damper/Silencer and duct installation - Lower Attenuator Room(B1/F)	7	0%	7	06-Sep-19	13-Sep-19					
SB-SVB-TVF-8											
SVB-TVF2440	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	06-Sep-19	12-Sep-19					
SVB-TVF2450	Damper/Silencer and duct installation - Lower Attenuator Room(B1/F)	7	0%	7	16-Sep-19	23-Sep-19					
SB-SVB-TVF-9											
SVB-TVF2480	Silencer, splitter and duct installation - Upper Attenuator Room (1/F)	6	0%	6	13-Sep-19	20-Sep-19					
B2/F											
SVB-EMB21010	E&M Installation - 1st fix - B2/F	25	0%	25	18-Mar-19 A	10-Aug-19					
SVB-EMB21060	E&M Installation - Electrical Plant Rooms- B2/F	40	0%	40	19-Aug-19	05-Oct-19					
SVB-EMB21080	E&M Installation - MVAC Palnt Rooms - B2/F	60	0%	60	05-Aug-19	16-Oct-19					
SVB-EMB21100	E&M Installation - FS Plant Rooms - B2/F	45	0%	45	17-Sep-19	09-Nov-19					
SVB-EMB21110	E&M Installation - PD Palnt Rooms - B2/F	60	0%	60	17-Sep-19	27-Nov-19					
B1/F											
SVB-EMB11000	E&M access to B1/F	0	0%	0	02-Jul-19						
SVB-EMB11010	E&M Installation - 1st fix - B1/F	25	0%	25	12-Jul-19	10-Aug-19					
SVB-EMB11020	E&M Installation - 2nd fix - B1/F	25	0%	25	10-Aug-19	09-Sep-19					
SVB-EMB11030	E&M Installation - Final fix - B1/F	25	0%	25	18-Sep-19	18-Oct-19					
SVB-EMB11060	E&M Installation - Electrical Plant Rooms - B1/F	40	0%	40	05-Aug-19	20-Sep-19					
SVB-EMB11080	E&M Installation - MVAC Plant Rooms - B1/F	60	0%	60	05-Aug-19	16-Oct-19					
SVB-EMB11100	E&M Installation - FS Plant Rooms - B1/F	48	0%	48	05-Aug-19	30-Sep-19					
SVB-EMB11120	E&M Installation - Elv Plant Rooms - B1/F	48	0%	48	05-Aug-19	30-Sep-19					
G/F											
SVB-EMGF1000	E&M access to G/F	0	0%	0	31-Jul-19						
SVB-EMGF1010	E&M Installation - 1st fix - G/F	25	0%	25	31-Jul-19	28-Aug-19					
SVB-EMGF1020	E&M Installation - 2nd fix - G/F	25	0%	25	29-Aug-19	27-Sep-19					
SVB-EMGF1050	E&M Installation - CLPP HV Switch Room - G/F	12	0%	12	05-Aug-19	17-Aug-19					
SVB-EMGF1060	Inspection & Handover to CLP	5	0%	5	19-Aug-19	23-Aug-19					
SVB-EMGF1070	Installation by CLP - CLPP HV Switch Room - G/F	24	0%	24	24-Aug-19	21-Sep-19					
SVB-EMGF1160	E&M Installation - MVAC Plant Rooms - G/F	40	0%	40	19-Aug-19	05-Oct-19					
SVB-EMGF1180	E&M Installation - FS Plant Rooms - G/F	40	0%	40	05-Aug-19	20-Sep-19					
SVB-EMGF1200	E&M Installation - PD Plant Rooms - G/F	40	0%	40	19-Aug-19	05-Oct-19					
SVB-EMGF1220	E&M Installation - Elv Plant Rooms - G/F	48	0%	48	05-Aug-19	30-Sep-19					
1/F											
SVB-EM1F1000	E&M access to 1/F	0	0%	0	30-Aug-19						
SVB-EM1F1010	E&M Installation - 1st fix - 1/F	25	0%	25	30-Aug-19	28-Sep-19					
SVB-EM1F1050	E&M Installation - 11kV Switch & Tx Room 1 - 1/F	41	0%	41	30-Aug-19	19-Oct-19					
SVB-EM1F1110	E&M Installation - 11kV Switch & Tx Room 2 - 1/F	41	0%	41	30-Aug-19	19-Oct-19					
SVB-EM1F1170	E&M Installation - LV Switch Room - 1/F	41	0%	41	04-Sep-19	25-Oct-19					
SVB-EM1F1220	E&M Installation - Electrical Plant Rooms - 1/F	50	0%	50	30-Aug-19	30-Oct-19					
SVB-EM1F1240	E&M Installation - MVAC Plant Rooms - 1/F	60	0%	60	30-Aug-19	11-Nov-19					
SVB-EM1F1260	E&M Installation - FS Plant Rooms - 1/F	50	0%	50	30-Aug-19	30-Oct-19					
SVB-EM1F1280	E&M Installation - ELV Plant Rooms - 1/F	50	0%	50	30-Aug-19	30-Oct-19					

Key Date 10 - FSD Building Structure & E&M Works

CONTRACT NO. HY2017/10
 NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
 THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 23/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019				
							Jun	Jul	Aug	Sep	
Building Structure											
FSD210	Ground Floor	20	50%	10	11-May-19 A	02-Jul-19					
FSD220	First Floor	25	0%	25	03-Jul-19	31-Jul-19					
FSD230	Roof Slab	25	0%	25	01-Aug-19	29-Aug-19					
FSD240	Top Roof	18	0%	18	30-Aug-19	20-Sep-19					
ABWF Works											
AFSD1000	Blockwork Walls	25	0%	25	15-Aug-19	12-Sep-19					
AFSD1010	Door and Window Frames	19	0%	19	22-Aug-19	12-Sep-19					
AFSD1020	ABWF Works to Plant Rooms G/F	56	0%	56	22-Aug-19	29-Oct-19					
AFSD1021	ABWF Works to Plant Rooms 1/F	56	0%	56	29-Aug-19	05-Nov-19					
AFSD1030	ABWF Works to Office and Corridors G/F	124	0%	124	22-Aug-19	20-Jan-20					
AFSD1031	ABWF Works to Office and Corridors 1/F	124	0%	124	29-Aug-19	30-Jan-20					
AFSD1040	ABWF Works to Toilets G/F	136	0%	136	22-Aug-19	06-Feb-20					
AFSD1050	Waterproofing and Roofing	52	0%	52	05-Sep-19	07-Nov-19					
AFSD1060	External Cladding and Wall Plastering	101	0%	101	05-Sep-19	07-Jan-20					
E&M Works											
Installation											
FSDB-EMGF0001	E&M cast-in Installation	80	50%	40	20-May-19 A	06-Aug-19					
G/F											
FSDB-EMGF104	ABWF Works ready for E&M Mobilization to CLP TX Room - G/F	0	0%	0	05-Sep-19						
FSDB-EMGF105	E&M Installation - CLP Tx Room - G/F	18	0%	18	05-Sep-19	26-Sep-19					
Statutory Inspections and approvals											
FSDB-SI1000	Submission of Genset Exhaust Drawing to EPD	0	0%	0	20-Jun-19						
FSDB-SI1005	Review and Approval of Genset Exhaust Drawing by EPD	48	0%	48	20-Jun-19	15-Aug-19					
Key Date 9 - C&ED Building & E&M Works											
Building Structure											
CED220	Ground Floor	20	55%	9	04-May-19 A	29-Jun-19					
CED230	First Floor	25	0%	25	02-Jul-19	30-Jul-19					
CED240	Second Floor	25	0%	25	31-Jul-19	28-Aug-19					
CED250	Third Floor	32	0%	32	29-Aug-19	08-Oct-19					
ABWF Works											
ACED1000	Blockwork Walls	54	0%	54	29-Aug-19	02-Nov-19					
ACED1010	Door and Window Frames	48	0%	48	05-Sep-19	02-Nov-19					
ACED1020	ABWF Works to Plant Rooms G/F	60	0%	60	12-Sep-19	23-Nov-19					
ACED1030	ABWF Works to Office and Corridors G/F	133	0%	133	12-Sep-19	24-Feb-20					
ACED1040	ABWF Works to Toilets G/F	142	0%	142	12-Sep-19	05-Mar-20					
E&M Works											
Installation											
C&EDB-GF0001	E&M cast-in Installation	90	40%	54	18-May-19 A	22-Aug-19					
Statutory Inspections and approvals											
C&EDB-SI1000	Submission of Genset Exhaust Drawing to EPD	0	0%	0	20-Jun-19						
C&EDB-SI1005	Review and Approval of Genset Exhaust Drawing by EPD	48	0%	48	20-Jun-19	15-Aug-19					
Key Date 11 - Landscape Soft Works & Trees Protection											
Trees Protection											
SL196	Protection Existing Trees & Submit Report with Photographic Record No.7	41	29.27%	29	05-Jun-19 A	24-Jul-19					
SL197	Protection Existing Trees & Submit Report with Photographic Record No.8	41	0%	41	25-Jul-19	10-Sep-19					
SL198	Protection Existing Trees & Submit Report with Photographic Record No.9	41	0%	41	11-Sep-19	31-Oct-19					
Key Date 8 - All Works for Tunnel Commissioning & Opening											

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 24/25

Date	Revision	Checked	Approved
20-Jun-19			

ID	Activity	Duration (Days)	% Comp	Remaining Duration	Start	Finish	2019			
							Jun	Jul	Aug	Sep
							Petrol Filling Station			
Structure										
PS110	Possess Portion Vc	0	0%	0	20-Jun-19					
PS120	Excavation	20	0%	20	20-Jun-19	13-Jul-19				
PS130	Footing	20	0%	20	15-Jul-19	06-Aug-19				
PS140	Petrol Filling Station Roof	14	0%	14	07-Aug-19	22-Aug-19				
PS150	Structure for Petrol Filling Station	36	0%	36	07-Aug-19	18-Sep-19				
PS160	Underground Fuel Tank Structure	36	0%	36	07-Aug-19	18-Sep-19				
PS170	Backfilling	20	0%	20	19-Sep-19	14-Oct-19				
E&M Works										
EPS110	Miscellaneous ABWF Works	42	0%	42	19-Sep-19	08-Nov-19				
EPS120	Fuel Tank/Fuel Pipe System Installation	42	0%	42	19-Sep-19	08-Nov-19				
Statutory Inspections and approvals										
Administration Building										
ADB-SI1000	Submission of Genset Exhaust Drawing to EPD	0	0%	0	20-Jun-19					
ADB-SI1005	Review and Approval of Genset Exhaust Drawing by EPD	48	0%	48	20-Jun-19	15-Aug-19				
Maintenance Depot										
MD-SI1000	Submission of Genset Exhaust Drawing to EPD	0	0%	0	20-Jun-19					
MD-SI1005	Review and Approval of Genset Exhaust Drawing by EPD	48	0%	48	20-Jun-19	15-Aug-19				
North Ventilation Building										
NVB-SI1000	Submission of Genset Exhaust Drawing to EPD	0	0%	0	20-Jun-19					
NVB-SI1005	Review and Approval of Genset Exhaust Drawing by EPD	48	0%	48	20-Jun-19	15-Aug-19				
Toll Control Building & Toll Collector Subway										
TCB-SI0010	Submission of Genset Exhaust Drawing to EPD	0	0%	0	20-Jun-19					
TCB-SI0015	Review and Approval of Genset Exhaust Drawing by EPD	48	0%	48	20-Jun-19	15-Aug-19				
Satellite Control Building										
SCB-SI1000	Submission of Genset Exhaust Drawing to EPD	0	0%	0	21-Jun-19					
SCB-SI1005	Review and Approval of Genset Exhaust Drawing by EPD	48	0%	48	21-Jun-19	17-Aug-19				
South Ventilation Building										
SVB-SI1000	Submission of Genset Exhaust Drawing to EPD	0	0%	0	24-Jun-19					
SVB-SI1005	Review and Approval of Genset Exhaust Drawing by EPD	48	0%	48	24-Jun-19	20-Aug-19				

CONTRACT NO. HY2017/10
NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS
THREE MONTHLY PROGRAMME AS OF 20 JUN 2019

P 25/25

Date	Revision	Checked	Approved
20-Jun-19			

Appendix C

Environmental Mitigation and Enhancement Measure Implementation Schedules

(In reference to CINOTECH (2011) Agreement No.
CE35/2011 EP Baseline Environmental Monitoring for
Hong Kong-Zhuhai-Macao Bridge Tuen Mun-Chek Lap
Kok Link - Investigation. Updated EM&A Manual for
Tuen Mun-Chek Lap Kok Link)

Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link
Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
Air Quality									
4.8.1	3.8	Watering of the construction sites in Lantau for 8 times/day and in Tuen Mun for 12 times/day to reduce dust emissions by 87.5% and 91.7% respectively and shall be undertaken.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		< >
4.8.1	3.8	The Contractor shall, to the satisfaction of the Engineer, install effective dust suppression measures and take such other measures as may be necessary to ensure that at the Site boundary and any nearby sensitive receiver, dust levels are kept to acceptable levels.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	The Contractor shall not burn debris or other materials on the works areas.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	In hot, dry or windy weather, the watering programme shall maintain all exposed road surfaces and dust sources wet.	All unpaved haul roads / throughout construction period in hot, dry or windy weather	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		< >
4.8.1	3.8	Where breaking of oversize rock/concrete is required, watering shall be implemented to control dust. Water spray shall be used during the handling of fill material at the site and at active cuts, excavation and fill sites where dust is likely to be created.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	Open dropping heights for excavated materials shall be controlled to a maximum height of 2m to minimise the fugitive dust arising from unloading.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	During transportation by truck, materials shall not be loaded to a level higher than the side and tail boards, and shall be dampened or covered before transport.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	No earth, mud, debris, dust and the like shall be deposited on public roads. Wheel washing facility shall be usable prior to any earthworks excavation activity on the site.	All site exits / throughout construction period	Contractor	TMEIA Avoid dust		Y		✓

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government

Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link
Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
4.8.1	3.8	Areas of exposed soil shall be minimised to areas in which works have been completed shall be restored as soon as is practicable.	All exposed surfaces / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	All stockpiles of aggregate or spoil shall be enclosed or covered and water applied in dry or windy condition.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.11	Section 3	EM&A in the form of 1 hour and 24 hour dust monitoring and site audit.	All representative existing ASRs / throughout construction period	Contractor	EM&A Manual		Y		N/A (Results adopted from published EM&A data of Contract No. HY/2012/08)
WATER QUALITY (LAND WORKS)									
6.10	-	Wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.10	-	Sewage effluent and discharges from on- site kitchen facilities shall be directed to Government sewer in accordance with the requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Temporary access roads should be surfaced with crushed stone or gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.10	-	Measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Open stockpiles of construction materials (e.g. aggregates and sand) on site should be covered with tarpaulin or similar fabric during rainstorms.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government

Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link
Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
6.10	5.8	Manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	All vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Wheel wash overflow shall be directed to silt removal facilities before being discharged to the storm drain.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.10	-	Vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for off site disposal.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.10	-	The Contractor shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Waste oil should be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance.	All areas/ throughout construction period	Contractor	TM-EIAO Waste Disposal Ordinance		Y		✓
6.10	-	All fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Surface run-off from bunded areas should pass through oil/grease traps prior to discharge to the stormwater system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.10	-	Roadside gullies to trap silt and grit shall be provided prior to	Roadside/design and operation	Design	TM-EIAO	Y		Y	N/A

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government

Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link
Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
		discharging the stormwater into the marine environment. The sumps will be maintained and cleaned at regular intervals.		Consultant/ Contractor					
6.10	Section 11	All construction works shall be subject to routine audit to ensure implementation of all EIA recommendations and good working practice.	All areas/ throughout construction period	Contractor	EM&A Manual		Y		✓
WASTE									
12.6		The Contractor shall identify a coordinator for the management of waste.	Contract mobilisation	Contractor	TMEIA		Y		✓
12.6		The Contractor shall prepare and implement a Waste Management Plan which specifies procedures such as a ticketing system, to facilitate tracking of loads and to ensure that illegal disposal of wastes does not occur, and protocols for the maintenance of records of the quantities of wastes generated, recycled and disposed. A recording system for the amount of waste generated, recycled and disposed (locations) should be established.	Contract mobilisation	Contractor	TMEIA, Works Branch Technical Circular No. 5/99 for the Trip-ticket System for Disposal of Construction and Demolition Material		Y		✓
12.6		The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges.	Contract mobilisation	Contractor	TMEIA, Land (Miscellaneous Provisions) Ordinance (Cap 28); Waste Disposal Ordinance (Cap 354); Dumping at Sea Ordinance (Cap 466); Water Pollution Control Ordinance.		Y		✓
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedures including waste reduction, reuse and recycling.	Contract Mobilisation	Contractor	TMEIA		Y		✓
12.6	8.1	The extent of cutting operation should be optimised where possible. Earth retaining structures and bored pile walls should be proposed to minimise the extent of cutting.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	The site and surroundings shall be kept tidy and litter free.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	No waste shall be burnt on site.	All areas / throughout construction period	Contractor	TMEIA		Y		✓

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government

Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link
Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
12.6	8.1	The Contractor shall be prohibited from disposing of C&D materials at any sensitive locations. The Contractor should propose the final disposal sites in the EMP and WMP for approval before implementation.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Stockpiled material shall be covered by tarpaulin and /or watered as appropriate to prevent windblown dust/ surface run off.	All areas / throughout construction period	Contractor	TMEIA		Y		<>
12.6	8.1	Excavated material in trucks shall be covered by tarpaulins to reduce the potential for spillage and dust generation.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Wheel washing facilities shall be used by all trucks leaving the site to prevent transfer of mud onto public roads.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Standard formwork or pre-fabrication should be used as far as practicable so as to minimise the C&D materials arising. The use of more durable formwork/plastic facing for construction works should be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should avoid over-ordering and wastage.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	The Contractor should recycle as many C&D materials (this is a waste section) as possible on-site. The public fill and C&D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials. Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	All falsework will be steel instead of wood.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Chemical waste producers should register with the EPD. Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows: f suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed; f Having a capacity of <450L unless the specifications have been approved by the EPD; and	All areas / throughout construction period	Contractor	TMEIA		Y		✓

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government

Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link
Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
		w Chinese according to the instructions prescribed in Schedule 2 of the Regulations. f Clearly labelled and used solely for the storage of chemical wastes; f Enclosed with at least 3 sides; f Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest; f Adequate ventilation; f Sufficiently covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and f Incompatible materials are adequately separated.							
12.6	8.1	Waste oils, chemicals or solvents shall not be disposed of to drain,	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Adequate numbers of portable toilets should be provided for on-site workers. Portable toilets should be maintained in reasonable states, which will not deter the workers from utilising them.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Night soil should be regularly collected by licensed collectors.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	General refuse arising on-site should be stored in enclosed bins or compaction units separately from C&D and chemical wastes. Sufficient dustbins shall be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station. Burning of refuse on construction sites is prohibited.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	All waste containers shall be in a secure area on hardstanding;	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Office wastes can be reduced by recycling of paper if such volume is sufficiently large to warrant collection. Participation in a local collection scheme by the Contractor should be advocated. Waste separation facilities for paper, aluminium cans, plastic bottles, etc should be provided on-site.	Site Offices/ throughout construction period	Contractor	TMEIA		Y		✓

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government

Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link
Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
12.6	Section 8	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.	All areas / throughout construction period	Contractor	EM&A Manual		Y		✓
LANDSCAPE AND VISUAL									
10.9	7.6	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas (Tree protection measures will be detailed at Tree Removal Application Stage) (CM1)	All areas/detailed design/during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme (CM2)	All areas/detailed design/during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Hillside and roadside screen planting to proposed roads, associated structures and slope works (CM3)	All areas/detailed design/during construction/post construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Hydroseeding or sheeting of soil stockpiles with visually unobstrusive material (in earth tone) (CM4)	All areas/detailed design/during construction/post construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works (CM5)	All areas/detailed design/during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Control night-time lighting and glare by hooding all lights (CM6)	All areas/detailed design/during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Ensure no run-off into water body adjacent to the Project Area (CM7)	All areas/detailed design/during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (CM8)	All areas/detailed design/during construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Recycle/ Reuse all felled trees and vegetation, e.g. mulching (CM9)	All areas/detailed design/during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government

Contract No. HY/2017/10
Tuen Mun – Chek Lap Kok Link
Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
10.9	7.6	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006 (CM10)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Re-vegetation of affected woodland/shrubland with native species (OM1)	All areas/detailed design/ during construction/ during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	n/a. To be implemented by AFCD/HyD/L CSD
10.9	7.6	Tall buffer screen tree / shrub / climber planting should be incorporated to soften hard engineering structures and facilities (OM2)	All areas/detailed design/ during construction/ during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	n/a. To be implemented by AFCD/HyD/L CSD
10.9	7.6	Streetscape elements (e.g. paving, signage, street furniture, lighting etc.) shall be sensitively designed in a manner that responds to the local context, and minimises potential negative landscape and visual impacts. Lighting units should be directional and minimise unnecessary light spill (OM3)	All areas/detailed design/ during construction / during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	n/a. To be implemented by HyD/LCSD
10.9	7.6	Structure, ornamental tree / shrub / climber planting should be provided along roadside amenity strips, central dividers and newly formed slopes to enhance the townscape quality and further greenery enhancement (OM4)	All areas/detailed design/ during construction / during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	n/a. To be implemented by HyD/LCSD
10.9	7.6	Aesthetically pleasing design (visually unobtrusive and non-reflective) as regard to the form, material and finishes	All areas/detailed design/ during construction / during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	n/a. To be implemented by HyD

*** Remarks:**

- ✓ Compliance of Mitigation Measures
- <> Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Contractor
- Δ Deficiency of Mitigation Measures but rectified by Contractor
- N/A Not Applicable in Reporting Period

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government

Appendix D

Summary of Action and Limit Levels

Table D1 *Action and Limit Levels for 1-hour and 24-hour TSP*

Parameters	Action	Limit
24 Hour TSP Level in $\mu\text{g}/\text{m}^3$	ASR1 = 213 ASR5 = 238 AQMS1 = 213 ASR6 = 238 ASR10 = 214	260
1 Hour TSP Level in $\mu\text{g} / \text{m}^3$	ASR1 = 331 ASR5 = 340 AQMS1 = 335 ASR6 = 338 ASR10 = 337	500

Appendix E

Event Action Plan

Appendix E1 Event/ Action Plan for Air Quality

EVENT	ET ⁽¹⁾	ACTION		
		IEC ⁽¹⁾	ER ⁽¹⁾	Contractor
Action Level				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify the source. 2. Inform the IEC and the ER. 3. Repeat measurement to confirm finding. 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET. 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice 2. Amend working methods if appropriate
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify the source. 2. Inform the IEC and the ER. 3. Repeat measurements to confirm findings. 4. Increase monitoring frequency to daily. 5. Discuss with the IEC and the Contractor on remedial actions required. 6. If exceedance continues, arrange meeting with the IEC and the ER. 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET. 2. Check the Contractor's working method. 3. Discuss with the ET and the Contractor on possible remedial measures. 4. Advise the ER on the effectiveness of the proposed remedial measures. 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify the Contractor. 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial actions to IEC within 3 working days of notification 2. Implement the agreed proposals 3. Amend proposal if appropriate

EVENT	ACTION			
	ET ⁽¹⁾	IEC ⁽¹⁾	ER ⁽¹⁾	Contractor
Limit Level				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify the source. 2. Inform the ER and the DEP. 3. Repeat measurement to confirm finding. 4. Increase monitoring frequency to daily. 5. Assess effectiveness of Contractor's remedial actions and keep the IEC, the DEP and the ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by the ET. 2. Check Contractor's working method. 3. Discuss with the ET and the Contractor on possible remedial measures. 4. Advise the ER on the effectiveness of the proposed remedial measures. 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify the Contractor. 3. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance 2. Submit proposals for remedial actions to IEC within 3 working days of notification 3. Implement the agreed proposals 4. Amend proposal if appropriate
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify the IEC, the ER, the DEP and the Contractor. 2. Identify the source. 3. Repeat measurements to confirm findings. 4. Increase monitoring frequency to daily. 5. Carry out analysis of the Contractor's working procedures to determine possible mitigation to be implemented. 6. Arrange meeting with the IEC and the ER to discuss the remedial actions to be taken. 7. Assess effectiveness of the Contractor's remedial actions 	<ol style="list-style-type: none"> 1. Discuss amongst the ER, ET and the Contractor on the potential remedial actions. 2. Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing. 2. Notify the Contractor. 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented. 4. Ensure remedial measures are properly implemented. 5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by the ER until the exceedance is abated.

and keep the IEC, the DEP and
the ER informed of the results.

8. If the exceedance stops, cease
additional monitoring.

Abbreviations: ET - Environmental Team, IEC - Independent Environmental Checker, ER - Engineer's Representative, DEP - Director of Environmental Protection

Appendix F

Monthly Summary of Waste Flow Table

Contract No. : HY/2017/10

**Tuen Mun Chek Lap Kok Link – Northern Connection Tunnel Buildings, Electrical and Mechanical Works
Monthly Summary Waste Flow Table for 2019 (Year)**

Month/Material	Actual Quantities of Inert C&D Materials Generation						Actual Quantities of C&D wastes Generation		Actual Quantities of Recyclables Generation			
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fills	Imported Fill	Chemical Waste	General Refuse	Metals	Felled trees	Paper/ cardboard packaging	Plastics
Unit	('000m ³)	('000m ³)	('000m ³)	('000m ³)	('000m ³)	('000m ³)	('000Kg)	('000Kg)	('000Kg)	('000Kg)	('000Kg)	('000Kg)
Jan	2.089	-	0.150	-	1.939	-	-	74.680	-	-	0.042	-
Feb	2.474	0.008	0.345	-	2.129	-	-	67.230	-	-	0.049	-
Mar	0.079	0.060	-	-	0.079	-	-	73.690	-	-	-	-
Apr	0.013	-	-	-	0.013	-	-	56.730	-	-	-	-
May	-	-	-	-	-	-	-	62.240	-	-	-	-
Jun	0.019	0.004	0.008	-	0.011	-	-	118.070	-	-	-	-
SUB-TOTAL	4.674	0.072	0.50	0.000	4.171	0.000	0.000	452.640	0.000	0.000	0.091	0.000
Jul	-	-	-	-	-	-	-	-	-	-	-	-
Aug	-	-	-	-	-	-	-	-	-	-	-	-
Sep	-	-	-	-	-	-	-	-	-	-	-	-
Oct	-	-	-	-	-	-	-	-	-	-	-	-
Nov	-	-	-	-	-	-	-	-	-	-	-	-
Dec	-	-	-	-	-	-	-	-	-	-	-	-
TOTAL	4.674	0.072	0.50	0.000	4.171	0.000	0.000	452.640	0.000	0.000	0.091	0.000

Notes :

- 1 - The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- 2 - Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- 3 - Broken concrete for recycling into aggregates.
- 4 - Assumed 5 kg per damaged water-filled barrier.
- 5 - Disposed as Public Fills includes Hard Rock and Large Broken Concrete.

Appendix G

Cumulative Statistics on
Exceedances, Complaints,
Notifications of Summons
and Successful Prosecutions

Appendix J1 Cumulative Statistics on Exceedances

		Total No. recorded in this reporting month	Total No. recorded since contract commencement
1-Hr TSP	Action	0	25
	Limit	0	2
24-Hr TSP	Action	0	2
	Limit	0	0

Appendix J2 Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Reporting Period	Cumulative Statistics		
	Complaints	Notifications of Summons	Successful Prosecutions
This Reporting Month (June 2018)	0	0	0
Total No. received since contract commencement	1	0	0
