

Contract No. HY/2012/08 Tuen Mun – Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section

Ninety-Fourth Monthly Environmental Monitoring & Audit (EM&A) Report

13 September 2021

Environmental Resources Management 2509, 25/F One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong Telephone 2271 3000 Facsimile 3015 8052





# Contract No. HY/2012/08 Tuen Mun – Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section

Ninety-Fourth Monthly Environmental Monitoring & Audit (EM&A) Report

Document Code: 0212330\_94th Monthly EM&A\_20210913.doc

#### Environmental Resources Management

2509, 25/F One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 3015 8052 E-mail: post.hk@erm.com http://www.erm.com

Client:		Project No	0:		
DBJV		021233	0		
Summary		Date:			
,		13 Sept	ember 20	)21	
		Approved	by:		
	ument presents the Ninety-Fourth Monthly EM&A Report Mun – Chek Lap Kok Link Northern Connection Sub-sea ection.	ling	2.1		
		Mr Crai	a Poid		
		Partner	y Neiu		
		Certified b	ov:		
		(	mill		
		Dr Jasn ET Leade			
	94 <sup>th</sup> Monthly EM&A Report	VAR	JN	CAR	13/09/21
Revision	Description	Ву	Checked	Approved	Date
name of 'EF terms of the Business ar	has been prepared by Environmental Resources Management the trading RM Hong-Kong, Limited', with all reasonable skill, care and diligence within the e Contract with the client, incorporating our General Terms and Conditions of id taking account of the resources devoted to it by agreement with the client. In any responsibility to the client and others in respect of any matters outside the e above.	Put	ernal		5 18001:2007 No. OHS 515956





#### Ref.: HYDHZMBEEM00\_0\_8550L.21

13 September 2021

By Fax (2293 6300) and By Post

AECOM Asia Co. Ltd. Supervising Officer Representative's Office No.8 Mong Fat Street, Tuen Mun, New Territories, Hong Kong

Attention: Mr. Roger Man

Dear Mr. Man,

#### Re: Agreement No. CE 48/2011 (EP) Environmental Project Office for the HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing Facilities, and Tuen Mun-Chek Lap Kok Link – Investigation

Contract No. HY/2012/08 TM-CLKL – Northern Connection Sub-sea Tunnel Section 94<sup>th</sup> Monthly EM&A Report for August 2021 (EP-354/2009/D)

Reference is made to the Monthly EM&A Report for August 2021 (ET's ref.: "0212330\_94th Monthly EM&A\_20210913.doc") certified by the ET Leader and provided to us via e-mail on 13 September 2021.

Please be informed that we have no adverse comments on the captioned Report. We write to verify the captioned submission in accordance with Condition 4.4 of EP-354/2009/D.

Thank you for your attention. Please do not hesitate to contact the undersigned or the ENPO Leader Mr. Y. H. Hui should you have any queries.

Yours sincerely,

Brian Tam Independent Environmental Checker Tuen Mun – Chek Lap Kok Link

c.c.

HyD	Mr. Patrick Ng	(By Fax: 3188 6614)
HyD	Mr. Alan Ip	(By Fax: 3188 6614)
AECOM	Mr. Conrad Ng	(By Fax: 3922 9797)
ERM	Dr. Jasmine Ng	(By Fax: 2723 5660)
DBJV	Mr. Bryan Lee	(By Fax: 2293 7499)

Internal: DY, YH, ENPO Site

Q:\Projects\HYDHZMBEEM00\02\_Proj\_Mgt\02\_Corr\2021\HYDHZMBEEM00\_0\_8550L.21.doc

TABLE OF CONTENTS

# EXECUTIVE SUMMARY

1

1	INTRODUCTION	3
1.1	BACKGROUND	3
1.2	Scope of Report	4
1.3	ORGANIZATION STRUCTURE	4
1.4	SUMMARY OF CONSTRUCTION WORKS	5
2	EM&A RESULTS	6
2.1	AIR QUALITY	6
2.2	WATER QUALITY MONITORING	6
2.3	DOLPHIN MONITORING	6
2.4	EM&A SITE INSPECTION	10
2.5	WASTE MANAGEMENT STATUS	10
2.6	ENVIRONMENTAL LICENSES AND PERMITS	11
2.7	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	13
2.8	SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMA	NCE
	Limit	13
2.9	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL	
	PROSECUTIONS	13
3	FUTURE KEY ISSUES	14
3.1	CONSTRUCTION ACTIVITIES FOR THE COMING MONTH	14
3.2	Key Issues for the Coming Month	14
3.3	MONITORING SCHEDULE FOR THE COMING MONTH	14
4	CONCLUSIONS AND RECOMMENDATIONS	15
4.1	Conclusions	15

APPENDIX A	PROJECT ORGANIZATION FOR ENVIRONMENTAL WORKS
Appendix B	CONSTRUCTION PROGRAMME
Appendix C	ENVIRONMENTAL MITIGATION AND Enhancement Measure Implementation Schedules
APPENDIX D	EM&A MONITORING SCHEDULES
Appendix E	OPERATIONAL PHASE DOLPHIN MONITORING Survey
APPENDIX F	CUMULATIVE STATISTICS ON EXCEEDANCES, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS
Appendix G	WASTE FLOW TABLE

# EXECUTIVE SUMMARY

Under *Contract No. HY/2012/08*, Dragages – Bouygues Joint Venture (DBJV) is commissioned by the Highways Department (HyD) to undertake the design and construction of the Northern Connection Sub-sea Tunnel Section of the Tuen Mun – Chek Lap Kok Link Project (TM-CLK Link Project) while AECOM Asia Company Limited was appointed by HyD as the Supervising Officer. For implementation of the environmental monitoring and audit (EM&A) programme under the Contract, ERM-Hong Kong, Limited (ERM) has been appointed as the Environmental Team (ET) in accordance with *Environmental Permit No. EP-354/2009/A*. Ramboll Hong Kong Ltd. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO). Subsequent applications for variation of environmental permits (VEP), *EP-354/2009/B*, *EP-354/2009/C* and *EP-354/2009/D*, were granted on 28 January 2014, 10 December 2014 and 13 March 2015, respectively.

The construction phase of the Contract commenced on 1 November 2013 and will tentatively be completed in 2021. The impact monitoring of the EM&A programme, including air quality, water quality, marine ecological monitoring and environmental site inspections, were commenced on 1 November 2013.

This is the Ninety-fourth Monthly EM&A report presenting the EM&A works carried out during the period from 1 to 31 August 2021 for the *Contract No. HY/2012/08 Northern Connection Sub-sea Tunnel Section* (the "Contract") in accordance with the Updated EM&A Manual of the TM-CLK Link Contract. As informed by the Contractor, there was no major activities undertaken in the reporting period.

Termination proposal for construction EM&A programme was approved by EPD on 19 March 2021. The construction phase EM&A programme of the Contract has been terminated since 19 March 2021.

In order to fulfil the EP's and EM&A Manual's requirements for TM-CLKL Project, Agreement No. HMWSD 1/2021 (EP) will take over the responsibility for implementation of operational phase dolphin monitoring from Contract No. HY/2012/08 from 1 September 2021 to 31 May 2022. A summary of monitoring and audit activities conducted in the reporting period is listed below:

Operational Phase Dolphin Monitoring 2 sessions

# Implementation of Marine Mammal Exclusion Zone

No marine works were undertaken during the reporting period, therefore, daily 250 m marine mammal exclusion zone monitoring was not undertaken during the reporting period.

# Summary of Breaches of Action/Limit Levels

# Breaches of Action and Limit Levels for Air Quality

No Action and Limit Level exceedance was recorded.

# Environmental Complaints, Non-compliance & Summons

No non-compliance with EIA recommendations, EP conditions and other requirements associated with the construction of this Contract was recorded in this reporting period.

No environmental complaint was received in this reporting period.

No environmental summons was received in this reporting period.

# Reporting Change

In order to fulfil the EP's and EM&A Manual's requirements for TM-CLKL Project, Agreement No. HMWSD 1/2021 (EP) will take over the responsibility for implementation of operational phase dolphin monitoring from Contract No. HY/2012/08 from 1 September 2021 to 31 May 2022.

# Upcoming Works for the Next Reporting Month

There are no major works to be undertaken in September 2021.

# Future Key Issue

There are no major works to be undertaken in September 2021.


#### 1.1 BACKGROUND

According to the findings of the Northwest New Territories (NWNT) Traffic and Infrastructure Review conducted by the Transport Department, Tuen Mun Road, Ting Kau Bridge, Lantau Link and North Lantau Highway would be operating beyond capacity after 2016. This forecast has been based on the estimated increase in cross boundary traffic, developments in the Northwest New Territories (NWNT), and possible developments in North Lantau, including the Airport developments, the Lantau Logistics Park (LLP) and the Hong Kong – Zhuhai – Macao Bridge (HZMB). In order to cope with the anticipated traffic demand, two new road sections between NWNT and North Lantau – Tuen Mun – Chek Lap Kok Link (TM-CLKL) and Tuen Mun Western Bypass (TMWB) are proposed.

An Environmental Impact Assessment (EIA) of TM-CLKL (the Project) was prepared in accordance with the EIA Study Brief (No. ESB-175/2007) and the *Technical Memorandum of the Environmental Impact Assessment Process (EIAO-TM*). The EIA Report was submitted under the Environmental Impact Assessment Ordinance (EIAO) in August 2009. Subsequent to the approval of the EIA Report (EIAO Register Number AEIAR-146/2009), an Environmental Permit (EP-354/2009) for TM-CLKL was granted by the Director of Environmental Protection (DEP) on 4 November 2009, and EP variation (VEP) (EP-354/2009/A) was issued on 8 December 2010. Subsequent applications for variation of environmental permits (VEPs), *EP-354/2009/B, EP-354/2009/C* and *EP-354/2009/D*, were granted on 28 January 2014, 10 December 2014 and 13 March 2015, respectively.

Under *Contract No. HY/2012/08*, Dragages – Bouygues Joint Venture (DBJV) is commissioned by the Highways Department (HyD) to undertake the design and construction of the Northern Connection Sub-sea Tunnel Section of TM-CLKL while AECOM Asia Company Limited was appointed by HyD as the Supervising Officer. For implementation of the environmental monitoring and audit (EM&A) programme under the Contract, ERM-Hong Kong, Limited (ERM) has been appointed as the Environmental Team (ET). Ramboll Hong Kong Ltd. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO).

Layout of the Contract components is presented in Figure 1.1.

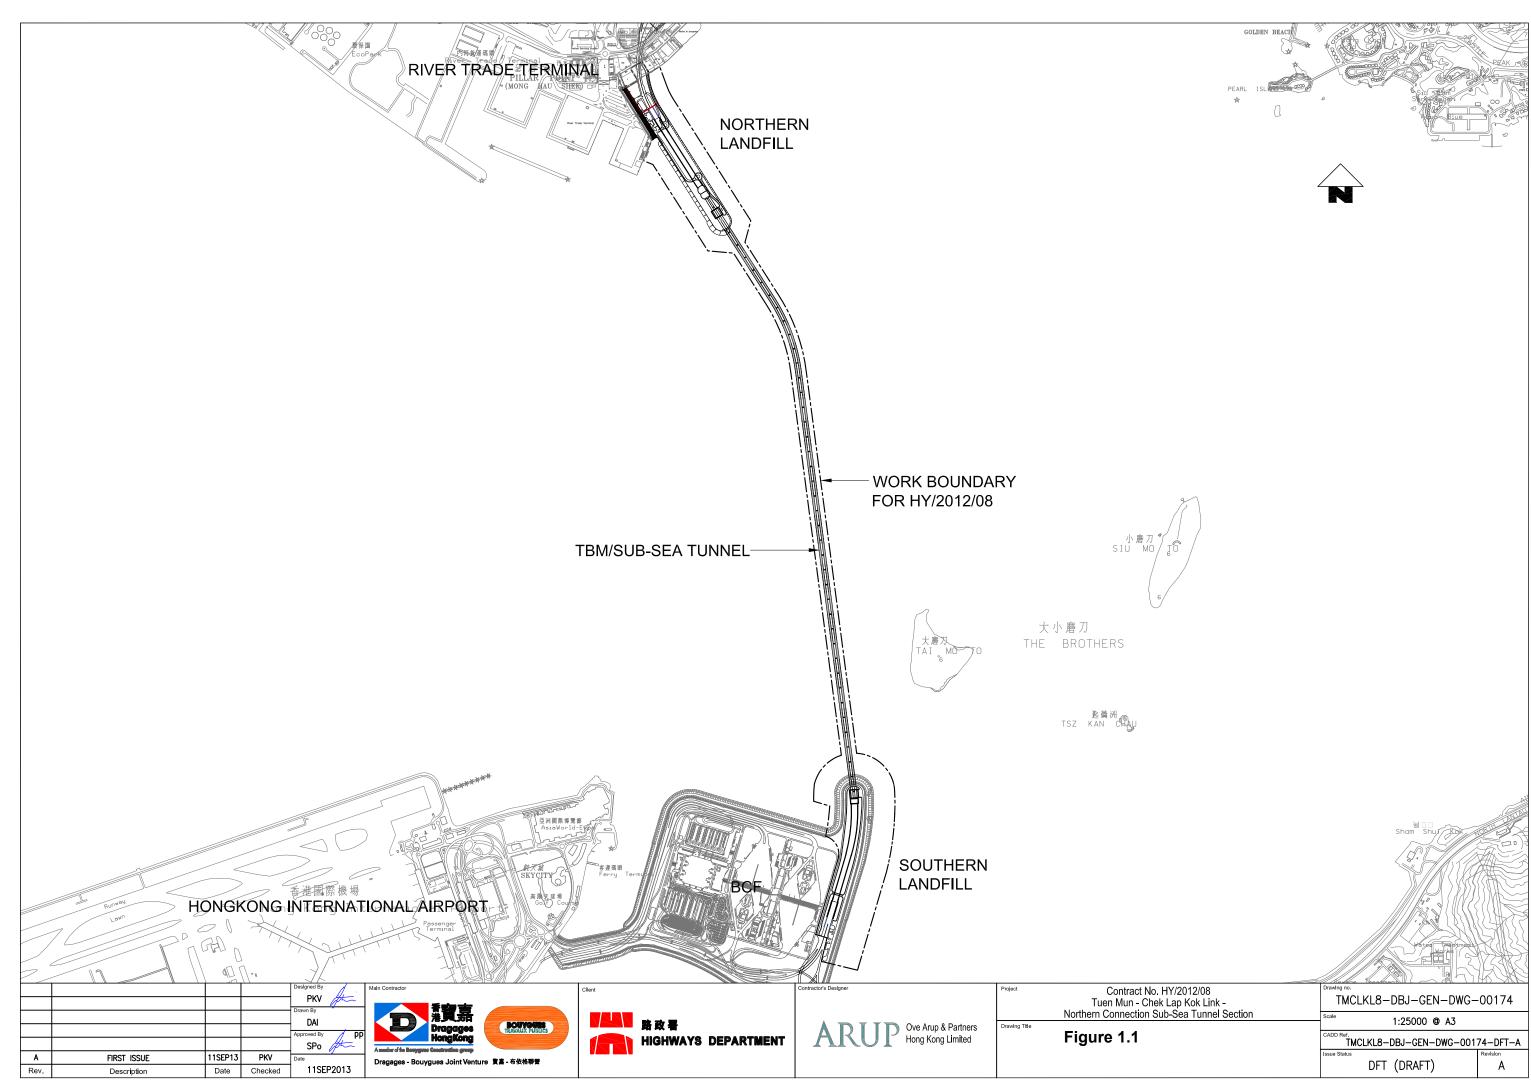

WING IS RETAINED BY THE ISSUER WHOSE CONSENT MUST BE OBTAINED BEFORE ANY USE OR REPRODUCTION OF THE DRAWING OR ANY PART THEREOF CAN BE MAD

The construction phase of the Contract commenced on 1 November 2013 and will tentatively be completed in 2021. The impact monitoring phase of the EM&A programme, including air quality, water quality, marine ecological monitoring and environmental site inspections, were commenced on 1 November 2013.

Termination proposal for construction EM&A programme was approved by EPD on 19 March 2021. The construction phase EM&A programme of the Contract has been terminated since 19 March 2021.

In order to fulfil the EP's and EM&A Manual's requirements for TM-CLKL Project, Agreement No. HMWSD 1/2021 (EP) will take over the responsibility for implementation of operational phase dolphin monitoring from Contract No. HY/2012/08 from 1 September 2021 to 31 May 2022.

### 1.2 SCOPE OF REPORT

This is the Ninety-fourth Monthly EM&A Report under the *Contract No. HY*/2012/08 *Tuen Mun – Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section.* This report presents a summary of the environmental monitoring and audit works in August 2021.

#### 1.3 ORGANIZATION STRUCTURE

The organization structure of the Contract is shown in *Appendix A*. The key personnel contact names and contact details are summarized in *Table 1.1* below.

# Table 1.1Contact Information of Key Personnel

Party	Position	Name	Telephone	Fax
Highways Department	Engr 24/SD	Ken T.M. Cheng	2762 4062	3188 6614
SOR (AECOM Asia Company Limited)	Senior Resident Engineer	K P Wong	2293 6403	2293 6300
ENPO / IEC (Ramboll Hong Kong Ltd.)	ENPO Leader	Y.H. Hui	3465 2850	3465 2899
	IEC	Brian Tam	9700 6767	3465 2899
Contractor (Dragages – Bouygues Joint Venture)	Quality and Environmental Manager	Erwin Regalado	2507 1732	2293 7499
	24-hour hotline		2293 7330	
ET (ERM-HK)	ET Leader	Jasmine Ng	2271 3311	2723 5660


#### 1.4 SUMMARY OF CONSTRUCTION WORKS

The construction phase of this Contract was commenced on 1 November 2013. The construction programme is shown in *Appendix B*.

As per DBJV's information, there was no major activities undertaken in the reporting period.

The Environmental Sensitive Receivers in the vicinity of the Contract are shown in *Figure 1.2*.

The implementation schedule of environmental mitigation measures is presented in *Appendix C*.

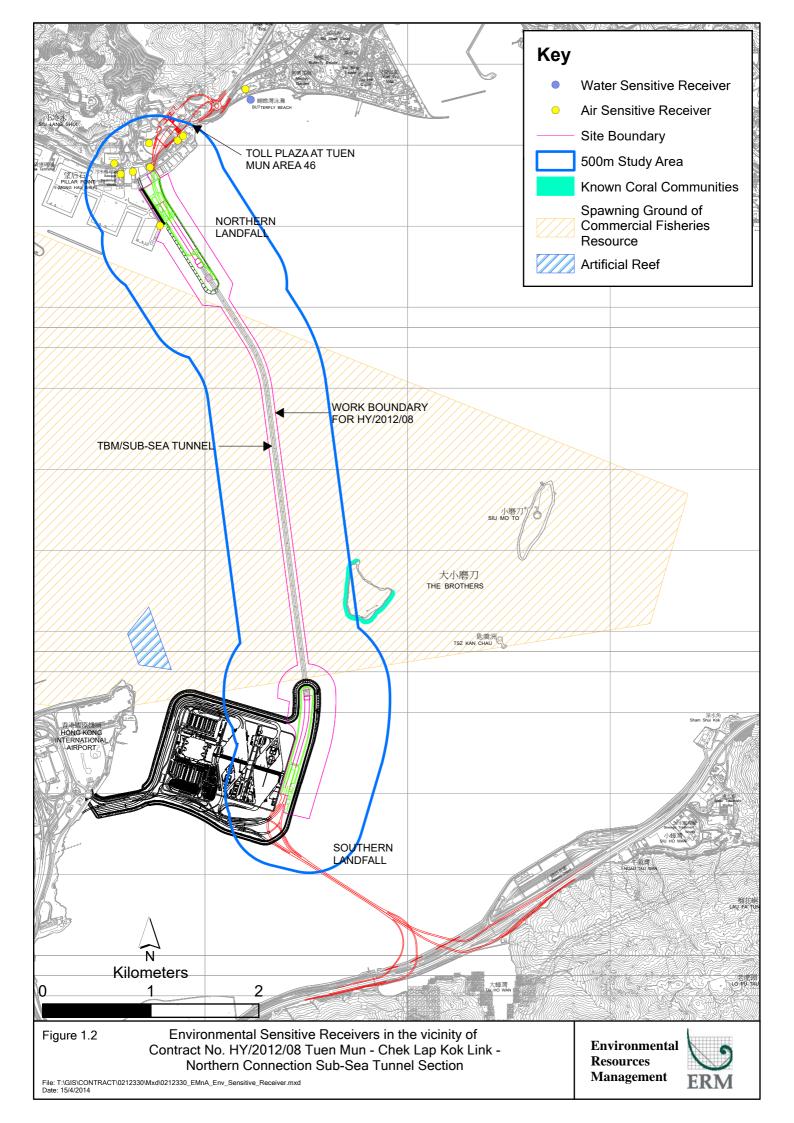

#### 2 EM&A RESULTS

The EM&A programme required environmental monitoring for air quality, water quality and marine ecology as well as environmental site inspections for air quality, noise, water quality, waste management, marine ecology and landscape and visual impacts. The EM&A requirements and related findings for each component are summarized in the following sections

#### 2.1 AIR QUALITY

Termination proposal for construction EM&A programme was approved by EPD on 19 March 2021. The construction phase EM&A programme of the Contract has been terminated since 19 March 2021.

#### 2.2 WATER QUALITY MONITORING

According to the Updated EM&A Manual, a operational phase water quality monitoring shall be performed monthly during the first year of Project operation at all designated monitoring stations including control stations. The operation phase water quality monitoring shall be ceased after the first year of operation of the Project subject to the first year review. Operational phase water quality monitoring commenced in June 2020 and completed in May 2021.

2.3 DOLPHIN MONITORING

#### 2.3.1 Monitoring Requirements

Operational Phase dolphin monitoring is required to be conducted by a qualified dolphin specialist team to evaluate whether there have been any effects on the dolphins. In order to fulfil the EM&A requirements and make good use of available resources, Contract No. HY/2012/08 has taken over the responsibility for implementation of dolphin monitoring from HZMB HKLR Contract No. HY/2011/03 since October 2019.

#### 2.3.2 Monitoring Equipment

*Table 2.1* summarises the equipment used for the operational phase dolphin monitoring.

#### Table 2.1Dolphin Monitoring Equipment

Equipment	Model
Global Positioning System (GPS)	Garmin 18X-PC
	Geo One Phottix
Camera	Nikon D90 300m 2.8D fixed focus
	Nikon D90 20-300m zoom lens

ENVIRONMENTAL RESOURCES MANAGEMENT 0212330\_94TH MONTHLY EM&A\_20210913.doc


Equipment	Model		
Laser Binocular	Infinitor LRF 1000		
Marine Binocular	Bushell 7 x 50 marine binocular with compass and reticules		
Vessel for Monitoring	65 foot single engine motor vessel with viewing platform 4.5m above water level		

# 2.3.3 Monitoring Parameter, Frequencies & Duration

Dolphin monitoring should cover all transect lines in Northeast Lantau (NEL) and the Northwest Lantau (NWL) survey areas twice per month throughout the entire construction period and operational phase. The monitoring data should be compatible with, and should be made available for, long-term studies of small cetacean ecology in Hong Kong. In order to provide a suitable long-term dataset for comparison, identical methodology and line transects employed in baseline dolphin monitoring was followed in the impact dolphin monitoring and operational phase dolphin monitoring.

# 2.3.4 Monitoring Location

The operational phase dolphin monitoring was carried out in the NEL and NWL along the line transect as depicted in *Figure 2.1*. The co-ordinates of all transect lines are shown in *Table 2.2* below.

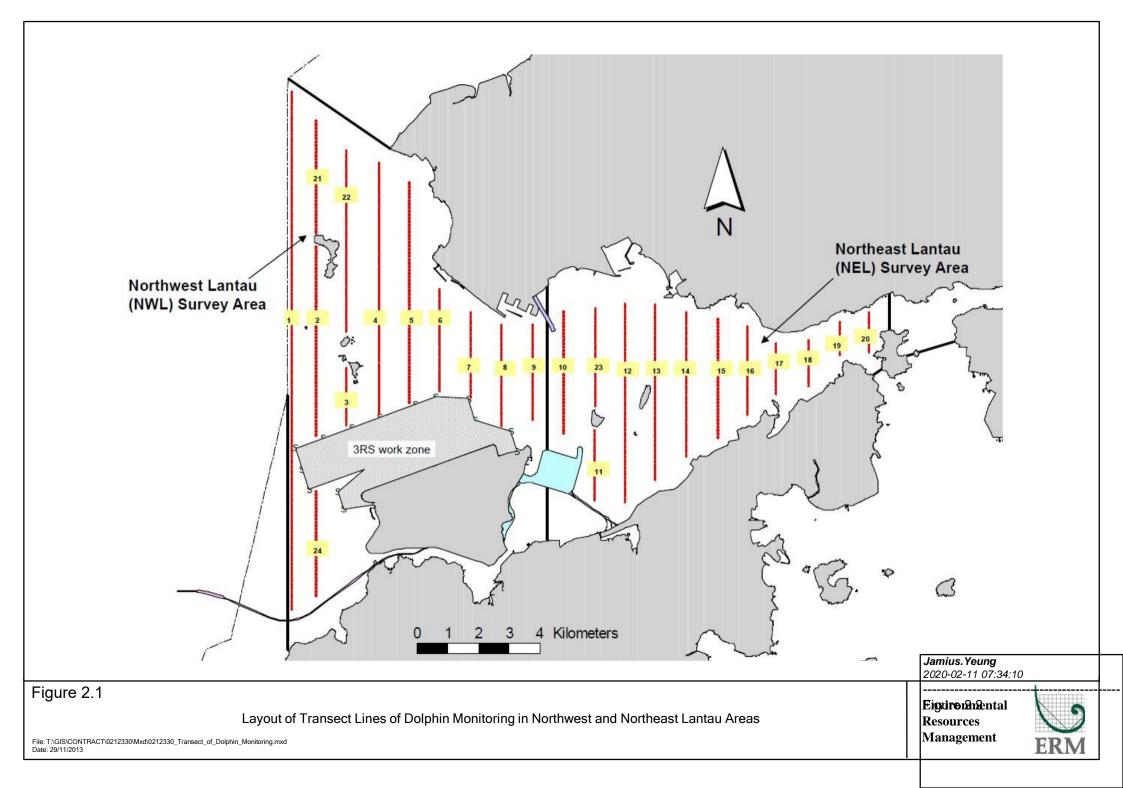

	Line No.	Easting	Northing		Line No.	Easting	Northing
1	Start Point	804671	815456	13	Start Point	816506	819480
1	End Point	804671	831404	13	End Point	816506	824859
2	Start Point	805476	820800*	14	Start Point	817537	820220
2	End Point	805476	826654	14	End Point	817537	824613
3	Start Point	806464	821150*	15	Start Point	818568	820735
3	End Point	806464	822911	15	End Point	818568	824433
4	Start Point	807518	821500*	16	Start Point	819532	821420
4	End Point	807518	829230	16	End Point	819532	824209
5	Start Point	808504	821850*	17	Start Point	820451	822125
5	End Point	808504	828602	17	End Point	820451	823671
6	Start Point	809490	822150*	18	Start Point	821504	822371
6	End Point	809490	825352	18	End Point	821504	823761
7	Start Point	810499	822000*	19	Start Point	822513	823268
7	End Point	810499	824613	19	End Point	822513	824321
8	Start Point	811508	821123	20	Start Point	823477	823402
8	End Point	811508	824254	20	End Point	823477	824613
9	Start Point	812516	821303	21	Start Point	805476	827081
9	End Point	812516	824254	21	End Point	805476	830562
10	Start Point	813525	821176	22	Start Point	806464	824033
10	End Point	813525	824657	22	End Point	806464	829598
11	Start Point	814556	818853	23	Start Point	814559	821739
11	End Point	814556	820992	23	End Point	814559	824768
12	Start Point	815542	818807	24*	Start Point	805476*	815900*
12	End Point	815542	824882	24*	End Point	805476*	819100*

# Table 2.2Operational Phase Dolphin Monitoring Line Transect Co-ordinates

Remarks: The coordinates of several starting and ending points have been revised due to the presence of a work zone to the north of the airport platform with intense construction activities in association with the construction of the third runway expansion for the Hong Kong International Airport. Co-ordinates in red and marked with asterisk are revised co-ordinates of transect line.

### 2.3.5 Monitoring Schedule for the Reporting Month

Dolphin monitoring was carried out on 3, 5, 9 and 24 August 2021. The dolphin monitoring schedule for the reporting month is shown in *Appendix D*.

### 2.3.6 Results & Observations

A total of 279.40 km of survey effort was collected, with 100% of the total survey effort being conducted under favourable weather conditions (i.e. Beaufort Sea State 3 or below with good visibility) in August 2021. Among the two areas, 109.90 km and 169.50 km of survey effort were collected from NEL and NWL survey areas, respectively. The total survey effort conducted on primary and secondary lines were 204.34 km and 75.06 km respectively. The survey efforts are summarized in *Appendix E*.

No Chinese White Dolphins was sighted in the two sets of surveys in August 2021.

No dolphin sighting was made in the proximity of the TM-CLKL alignment.

Encounter rates of Chinese White Dolphins are deduced from the survey effort and on-effort sighting data made under favourable conditions (Beaufort 3 or below) in August 2021 with the results present in *Tables 2.3* and *2.4*.

<i>Tuble 2.5 Inutotulual Survey Event Encounter Kales</i>	Table 2.3	Individual Survey Event Encounter Rates
---	-----------	---

		Encounter rate (STG)	Encounter rate (ANI)
		(no. of on-effort dolphin	(no. of dolphins from all on-
		sightings per 100 km of	effort sightings per 100 km of
		survey effort)	survey effort)
		Primary Lines Only	Primary Lines Only
NEL	Set 1: August 3rd / 5th	0.0	0.0
INEL	Set 2: August 9th / 24th	0.0	0.0
NWL	Set 1: August 3rd / 5th	0.0	0.0
INVIL	Set 2: August 9th / 24th	0.0	0.0

Note: Dolphin Encounter Rates are deduced from the Two Sets of Surveys (Two Surveys in Each Set ) in August 2021 in Northeast (NEL) and Northwest Lantau (NWL)

# Table 2.4Monthly Average Encounter Rates

	(no. of on-ef) sightings per 10	rate (STG) fort dolphin 00 km of survey ort)	(no. of dolphi effort sighting	ncounter rate (ANI) of dolphins from all on- sightings per 100 km of survey effort)	
	Primary Lines Only	Both Primary and Secondary Lines	Primary Both Prima Lines Only and Second Lines		
Northeast Lantau	0.0	0.0	0.0	0.0	
Northwest Lantau	0.0	0.0	0.0	0.0	

Note: Overall dolphin encounter rates (sightings per 100 km of survey effort) from all four surveys are conducted in August 2021 on primary lines only as well as both primary lines and secondary lines in Northeast and Northwest Lantau.

According to the EM&A Manual, Operational Phase Monitoring on dolphin monitoring shall be undertaken based upon the frequency of forty-eight, oneday survey events at a frequency of 2 per month over a period of 24 months following cessation of the construction. The schedule for operational phase monitoring on dolphin monitoring in August 2021 is provided in Appendix D.

In order to fulfil the EP's and EM&A Manual's requirements for TM-CLKL Project, Agreement No. HMWSD 1/2021 (EP) will take over the responsibility for implementation of operational phase dolphin monitoring from Contract No. HY/2012/08 from 1 September 2021 to 31 May 2022.

#### 2.3.7 Implementation of Marine Mammal Exclusion Zone

No marine works were undertaken during the reporting period, therefore, daily 250 m marine mammal exclusion zone monitoring was not undertaken during the reporting period.

#### 2.4 EM&A SITE INSPECTION

Termination proposal for construction EM&A programme was approved by EPD on 19 March 2021. The construction phase EM&A programme of the Contract has been terminated since 19 March 2021.

#### 2.5 WASTE MANAGEMENT STATUS

The Contractor had submitted application form for registration as chemical waste producer under the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.

Wastes generated during this reporting period included mainly construction wastes (inert and non-inert). Reference has been made to the waste flow table prepared by the Contractor (*Appendix G*). The quantities of different types of wastes are summarized in Table 2.5.

#### Table 2.5 Quantities of Different Waste Generated in the Reporting Month

Month/Year	Inert Construction	Inert Construction	Non-inert Construction	Recyclable Materials <sup>(c)</sup>	Chemical Wastes	Ma	rine Sediment	(m³)
	Waste <sup>(a)</sup> (tonnes)	Waste Re- used (tonnes)	Waste <sup>(b)</sup> (tonnes)	(kg)	(kg)	Category L	Category M (M <sub>p</sub> & M <sub>f</sub> )	Mixed (L+M)
August 2021	17	0	7	0	0	0	0	0

Notes:

(a) Inert construction wastes include hard rock and large broken concrete, and materials disposed as public fill.

(b) Non-inert construction wastes include general refuse disposed at landfill.

(c) Recyclable materials include metals, paper, cardboard, plastics, timber and others.

The Contractor was advised to properly maintain on site C&D materials and waste collection, sorting and recording system, dispose of C&D materials and wastes at designated ground and maximize reuse/ recycle of C&D materials and wastes. The Contractor was also reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly For chemical waste containers, the Contractor was reminded to treat properly and store temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.

### 2.6 Environmental Licenses and Permits

The status of environmental licensing and permit is summarized in *Table 2.6* below.

License/ Permit	License or Permit No.	Date of Issue	Date of Expiry	License/ Permit Holder	Remarks
Environmental Permit	EP-354/2009/D	13 March 2015	Throughout the Contract	HyD	Application for VEP on 3 March 2015 to
					supersede EP-354/2009/C
Construction Dust	435068	27 June 2018	Throughout the Contract	DBJV	Northern Landfall
Notification					
Construction Dust	435505	12 July 2018	Throughout the Contract	DBIV	Southern Landfall
Notification	100000	12 July 2010	inoughout the contract		
Chemical Waste	5213-422-D2516-02	18 January 2017	Throughout the Contract	DBJV	Northern Landfall
Registration					
Chemical Waste	5213-951-D2591-01	25 May 2016	Throughout the Contract	DBJV	Southern Landfall
Registration		<b>a</b> a <b>k a</b> a <b>ta</b>		557 I	
Construction Waste	7018108	28 August 2013	Throughout the Contract	DBJV	Waste disposal in Contract No. HY/2012/08
Disposal Account Waste Water Discharge	WT00031435-2018	2 August 2018	31 August 2023	DBIV	Southern Landfall
License	VV 100051455-2010	2 Mugust 2010	51 August 2025	DDJV	Southern Lanutan
Waste Water Discharge	WT00034060-2019	25 July 2019	30 June 2024	DBJV	Northern Landfall (4 Discharge Point)
License				,	、 0 <i>,</i>

# Table 2.6Summary of Environmental Licensing and Permit Status


Notes:

HyD = Highways Department

DBJV = Dragages – Bouygues Joint Venture

VEP = Variation of Environmental Permit

2.7	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES
	A summary of the Implementation Schedule of Environmental Mitigation Measures (EMIS) is presented in <i>Appendix C</i> . The necessary mitigation measures relevant to this Contract were implemented properly.
2.8	SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMANCE LIMIT
	No Action and Limit Level exceedance of was recorded.
	Cumulative statistics are provided in <i>Appendix F</i> .
2.9	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS
	The Environmental Complaint Handling Procedure is provided in Figure 2.2.
	No environmental complaint was received in this reporting period.
	No environmental summons was received in this reporting period.
	Statistics on complaints, notifications of summons and successful prosecutions are summarized in <i>Appendix F</i> .

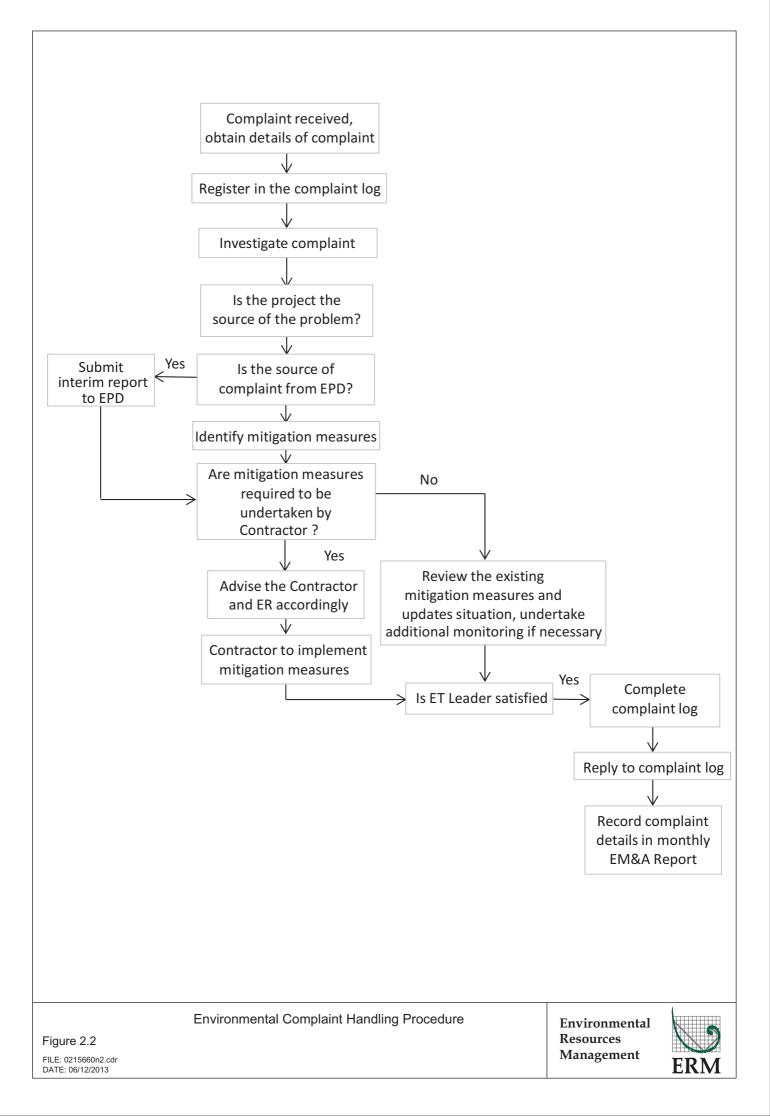

### *3 FUTURE KEY ISSUES*

#### 3.1 CONSTRUCTION ACTIVITIES FOR THE COMING MONTH

There are no major works to be undertaken in September 2021.

#### 3.2 KEY ISSUES FOR THE COMING MONTH

There are no major works to be undertaken in September 2021.

### 3.3 MONITORING SCHEDULE FOR THE COMING MONTH

In order to fulfil the EP's and EM&A Manual's requirements for TM-CLKL Project, Agreement No. HMWSD 1/2021 (EP) will take over the responsibility for implementation of operational phase dolphin monitoring from Contract No. HY/2012/08 from 1 September 2021 to 31 May 2022.

#### 4 CONCLUSIONS AND RECOMMENDATIONS

#### 4.1 CONCLUSIONS

This Ninety-fourth EM&A Report presents the findings of the EM&A activities undertaken during the period from 1 to 31 August 2021, in accordance with the Updated EM&A Manual and the requirements of EP-354/2009/D.

Operational phase dolphin monitoring were carried out in this reporting month.

No Action and Limit Level exceedance was recorded.

No Chinese White Dolphins was sighted in the two sets of surveys in August 2021.

No non-compliance event was recorded during the reporting period.


No environmental complaint was received in this reporting period.

No environmental summons was received in this reporting period.

Termination proposal for construction EM&A programme was approved by EPD on 19 March 2021. The construction phase EM&A programme of the Contract has been terminated since 19 March 2021.

In order to fulfil the EP's and EM&A Manual's requirements for TM-CLKL Project, Agreement No. HMWSD 1/2021 (EP) will take over the responsibility for implementation of operational phase dolphin monitoring from Contract No. HY/2012/08 from 1 September 2021 to 31 May 2022. Appendix A

Project Organization for Environmental Works

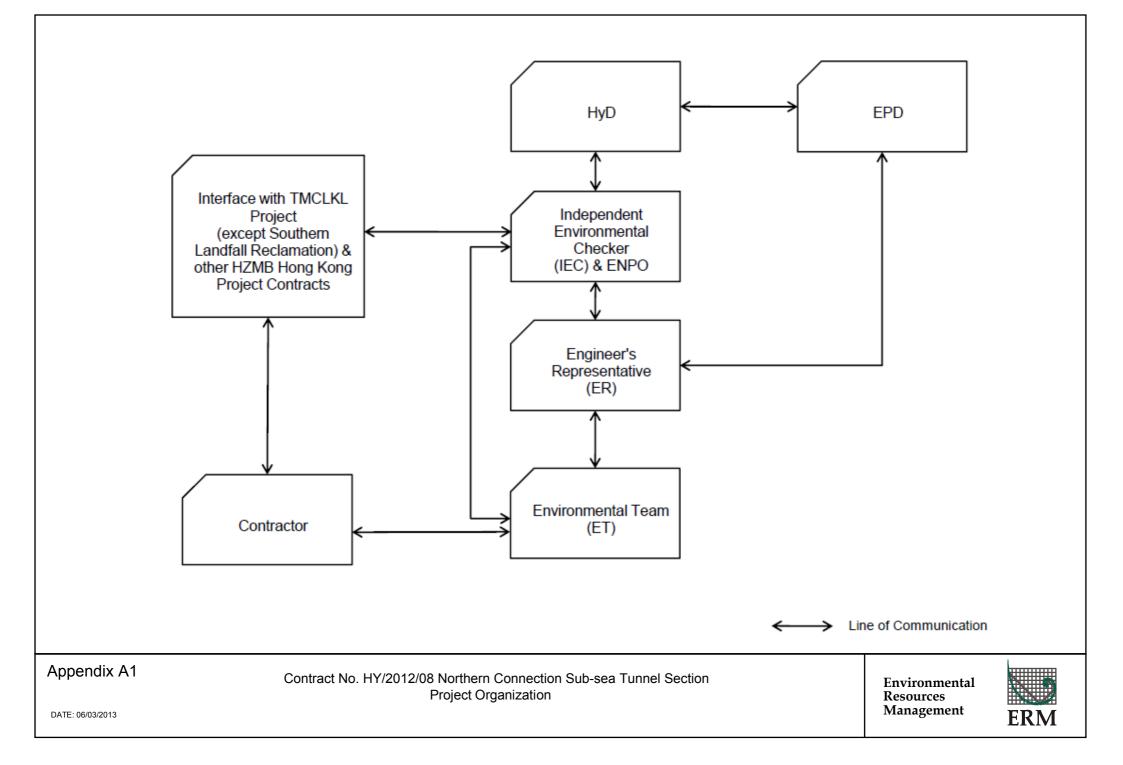

Appendix B

Construction Programme

#	Activity Name	Orig	Start	Finish	Target Finish					2020	
		Dur			Date	23 01	March	April   29   05   12   19   26	May 03   10   17   24	June         July         August           31         07         14         21         28         05         12         19         26         02         09         16	September         October         November           23         30         06         13         20         27         04         11         18         25         01         08         15         22         i
1	TMCLKL Northen Connection Sub-sea Tunnel Section	217	24-Feb-20	14-Nov-20							
2	Contract Key Date	8	05-May-20	14-May-20					Contrac	t Key Date	Progress as of: 23 Aug 20
3	[KD-3c] Stage 3c Completion - SLF UU & At-grade works provision	0		14-May-20					◆ [KD-3c]	Stage 3c Completion - SLF UU & At-grade worl	s provision
4	[KD-9] Section 2 Completion - Tunnel & Approach Ramp	0		05-May-20				ig activities after	[KD-9] Section	n 2 Completion - Tunnel & Approach Ramp	
5	[KD-12] Section 4 Completion - SLF At-grade Road	0		14-May-20			14 May 2		♦ [KD-12]	Section 4 Completion - SLF At-grade Road	
6	[KD-13] Section 5 Completion - Preservation and Protection of Trees	0		14-May-20			14 May 2	020	◆ [KD-13]	Section 5 Completion - Preservation and Prote	
/	Northern Landfall Remaining Works	228	24-Feb-20	14-Nov-20							Outstanding activities after Vorther
8	CLP Substation preparation for De-energization	46	24-Feb-20	16-Apr-20				CLP S	ubstation prepara	tion for De-energization	substantial completion on
9 10	CLP Substation - Dismantling, Removal & Reinstatement Drainage & U Channel Installation	39 50	01-Oct-20 31-Mar-20	14-Nov-20 27-May-20					·····	Prainage & U Channel Installation	02 Jun 2020
11	Chain Fence & Reinstatement at Box Culvert (VO)		23-May-20	30-May-20	30-Sep-20					Chain Fence & Reinstatement at Box Culvert (	VO) (Y-shape modification & Maintenance Access)
12	NLF U Channel Cover Installation	38	17-Apr-20	30-May-20	15-Sep-20					· · · · · · · · · · · · · · · · · · ·	(Pending Handover Inspection)
13	Sewerage Pump Sump RC Structure	40	15-Apr-20	30-May-20						Sewerage Pump Sump RC Structure	
14	Sewerage Pump Sump Pipe Connection	12	01-Jun-20	13-Jun-20						Sewerage Pump Sump Pipe Connecti	
15	Penstock & Actuator (C4 Interface)	7	31-Jul-20	07-Aug-20							ck & Actuator (C4 Interface)
16 17	NLF Footpath NLF Traffic Sign	32 40	13-Apr-20 15-Apr-20	19-May-20 30-May-20	15-Auq-20					Footpath NLF Traffic Sign	
18	New Road layout at C2/C3 after Bus Trial (VO)	38	02-May-20	15-Jun-20	107100 20				÷;;	New Road layout at C2/C3 after Bus	Frial (VO)
19	Carpark Canopy (6 nos)	40	15-Apr-20	30-May-20					-iiii	Carpark Canopy (6 nos)	
20	Portal Pump Sump hard paving and footpath	12	29-Apr-20		05-Sep-20					imp Sump hard paving and footpath	(Planter Wall Design Issue)
21	NVB Green Roof Planting (subject to C4 water supply)	24	01-Jul-20	28-Jul-20	30-Sep-20					NVB Green	Roof Planting (subject to C4 water supply)
22	Tunnel Internal Structure	95	13-Apr-20	31-Jul-20						i i i i i i i i i i i	rnal Structure (Subject to permanent water supply by
23	Access Hatch Installation	24	21-Apr-20	18-May-20						s Hatch Installation	Пистору
24	Manhole, Multipart Cover Installation & Cleaning	18	13-Apr-20	02-May-20	7 4 00				Manhole, Mult	part Cover Installation & Cleaning	
25 26	TSA NCR - Parapet Extension	23	18-May-20	12-Jun-20	7-Aug-20					TSA NCR - Parapet Extension	
20	Gully Cover Installation CCTV Testing	36 36	20-Apr-20 20-Apr-20	30-May-20 30-May-20	15-Aug-20				******	Gully Cover Installation	(Repair works on going)
28	TNA Cross Road Drainage Pipe from Cable Through	18	11-May-20	30-May-20	8-Jul-20					TNA Cross Road Drainage Pipe from Cable Ti	rough
29	TSA Cross Road Drainage Pipe from Cable Through	19	01-Jun-20	22-Jun-20	4-Jul-20					TSA Cross Road Drainage Pipe f	om Cable Through
30	Low Point Pump Sump Installation	36	20-Apr-20	30-May-20	15-Aug-20					Low Point Pump Sump Installation	
31	Additional Pump installation	18	01-Jun-20	20-Jun-20	15-Aug-20		-++		·····	Additional Pump installation	
32	SHMS Site Installation Works	14	15-May-20	30-May-20	15-Aug-20					SHMS Site Installation Works	ing & Commissioning
33 34	SHMS Testing & Commissioning Southern Landfall Remaining Works	53 210	01-Jun-20 24-Feb-20	31-Jul-20 24-Oct-20	15-Oct-20		· · · · · · · · · · · · · · · · · · ·			, SHIMS, IES	Southern Landfall F
	¥								·····		V Outrient Landian i
35 36	Landscape Formation Cell 1 Omega Seal Installation	79 50	24-Feb-20 02-Apr-20	25-May-20 29-May-20						andscape Formation Cell 1 Omega Seal Installation	
37	Overall Road Lighting Ducting	38	02-Apr-20 08-Apr-20	29-101ay-20 21-May-20					Ove	erall Road Lighting Ducting	
38	Drainage West Side + U Channel outstanding	34	08-Apr-20	16-May-20						ge West Side + U Channel outstanding	
39	Drainage East side & Central location + U Channel	84	24-Feb-20	30-May-20						Drainage East side & Central location + U Cha	nnel
40	Sign Plate Installation	37	15-Apr-20	27-May-20						Sign Plate Installation	
41	Carpark Construction (Impact by C4)	46	20-Apr-20	11-Jun-20						Carpark Construction (Impact by C4)	
42 43	SHMS (Structural Health Monitoring System) V083 Maintenance foothpath along HKBCF fencing	45	09-Apr-20	30-May-20 26-May-20	_26-Aug-20					01111/S (Structural Health Monitoring System) (083 Maintenance foothpath along HKBCF fence	(TI:AISSUE)
43	V083 Maintenance roompain along HKBCP rending	20 16	04-May-20 08-May-20	26-May-20 26-May-20	·				_	123 SCB Directional Sign	<u>19</u>
45	Paving Block	54	20-Apr-20	20-Jun-20					······································	Paving Block	
46	Ramp F Reinstatement	73	01-Aug-20	24-Oct-20							Ramp F Reinstaten
47	Pump Sump Installation	81	24-Feb-20	27-May-20			· · · · · · · · · · · · · · · · · · ·	+ + + + +		Pump Sump Installation	
48	SAR Remaining Activities	85	24-Feb-20	01-Jun-20	15 0 00		- +			SAR Remaining Activities	
49	SVB Green Roof Planting (subject to C4 water supply)	26	15-Jul-20	13-Aug-20	15-Sep-20			· · · · · · · · · · · · · · · · · · ·		Seawall & C66 Reinstatement	B Green Roof Planting (subject to C4 water supply) (Subject to permanent water supply by mid-Sep)
50 51	Seawall & C66 Reinstatement Overall Pavement Works	54 216	30-Mar-20 24-Feb-20	30-May-20 31-Oct-20					· · · · · · · · · · · · · · · · · · ·		Overall Pavem
										and baced	
52 53	1st Layer Road base 2nd & 3rd Layer Road base	63 89	24-Feb-20 24-Feb-20	06-May-20 05-Jun-20			- <u>.</u>		1st Layer Ro	2nd & 3rd Layer Road base	
54	Base Course	100	24-Feb-20	18-Jun-20					· · · · · · · · · · · · · · · · · · ·		(CLP Storage)
55	PMBSMA / Wearing Course	64	01-Aug-20	14-Oct-20							PMBSMA / Wearing Cou
56	Overall Road Marking	64	19-Aug-20	31-Oct-20							Overall Road N
57	AOB Items	182	24-Feb-20	22-Sep-20							✓ AOB Items
58	Electrical Vehicle confirmation from supplier	72	24-Feb-20	16-May-20					Electri	cal Vehicle confirmation from supplier	
59	Electrical Vehicle Fabrication & Delivery	110	18-May-20	22-Sep-20							Electrical Vehicle Fabrication & Delive
60	WA 23 Clearance for Spoil removal	72	11-May-20	01-Aug-20						WA 23 Cle	erance for Spoil removal
61	WA 23 Reinstatement	36	03-Aug-20	12-Sep-20	5 Sep-20				·····	Notth 9 Oc	WA 23 Reinstatement uth Tunnel Portal Naming Frame
62	North & South Tunnel Portal Naming Frame	27	01-Jul-20	31-Jul-20							
Page 1	of 1	t		TMCLK	Northern	Conn	ection Sub	-sea Tunnel S	ection		Date         Revision         Checked         Approved           19-May-20         For Monitoring         SPa         DLo
Data D	ate: 24-Feb-20 Northern Landfall AOB				_						
Data D	ate: 24-Feb-20				Program	nme o	of Remainii	ng Works		Dragages HongKong	
	Southern Landfall				-		· · · - ·		A	A member of the Bouygues Construction group	
					Forecas	t as c	of: 24 Febru	uary 2020		Dragages - Bouyques Joint Venture 寶嘉 - 布依格聯營	

Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

Appendix C

Environmental Mitigation and Enhancement Measure Implementation Schedules

EIA Reference	EM&A Manual		Location/ Timing	Implementation Agent	Relevant Standard or Requirement		olementa Stages		Status *
	Reference					D	C	0	
Air Quality					_			_	
4.8.1	3.8	An effective watering programme of twice daily watering with complete coverage, is estimated to reduce by 50%. This is recommended for all areas in order to reduce dust levels to a minimum;		Contractor	TMEIA Avoid smoke impacts and disturbance		Y		N/A
4.8.1	3.8	Watering of the construction sites in Lantau for 8 times/day and in Tuen Mun for 12 times/day to reduce dust emissions by 87.5% and 91.7% respectively and shall be undertaken.	, 0	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	The Contractor shall, to the satisfaction of the Engineer, install effective dust suppression measures and take such other measures as may be necessary to ensure that at the Site boundary and any nearby sensitive receiver, dust levels are kept to acceptable levels.	construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	The Contractor shall not burn debris or other materials on the works areas.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	In hot, dry or windy weather, the watering programme shall maintain all exposed road surfaces and dust sources wet.	All unpaved haul roads / throughout construction period in hot, dry or windy weather	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		N/A
4.8.1	3.8	Where breaking of oversize rock/concrete is required, watering shall be implemented to control dust. Water spray shall be used during the handling of fill material at the site and at active cuts, excavation and fill sites where dust is likely to be created.	construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	Open dropping heights for excavated materials shall be controlled to a maximum height of 2m to minimise the fugitive dust arising from unloading.	construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	During transportation by truck, materials shall not be loaded to a level higher than the side and tail boards, and shall be dampened or covered before transport.		Contractor	TMEIA Avoid dust generation		Y		N/A

EIA Reference	Manual		Location/ Timing	Implementation Agent	Relevant Standard or Requirement		olementa Stages		Status *
	Reference					D	C	0	
4.8.1	3.8	Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards.	construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	No earth, mud, debris, dust and the like shall be deposited on public roads. Wheel washing facility shall be usable prior to any earthworks excavation activity on the site.	. 0	Contractor	TMEIA Avoid dust		Y		N/A
4.8.1	3.8	Areas of exposed soil shall be minimised to areas in which works have been completed shall be restored as soon as is practicable.	All exposed surfaces / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.8.1	3.8	All stockpiles of aggregate or spoil shall be enclosed or covered and water applied in dry or windy condition.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		N/A
4.11	Section 3	EM&A in the form of 1 hour and 24 hour dust monitoring and site audit.	All representative existing ASRs / throughout construction period	Contractor	EM&A Manual		Y		N/A
WATER QUAI	LITY								
Marine Works (Se	quence A)								
6.1	Annex A	Construction of seawalls to be advanced by at least 200m before the main reclamation dredging and filling can commence. The protection by advanced seawall is a dynamic process depending on the progress of the construction activities and the stage when such protection could be realised is illustrated in Figure 6.2a and detailed in Appendix D6a. The part of the works where such measures can be undertaken for the majority of the time includes the following locations:	backfilling works	Contractor	TM-EIAO		Y		N/A
Figure 6.2a		iocutions.							
Appendix D6a		- TM-CLKL northern reclamation;							
6.1	-	a maximum of 50% public fill to be used for all seawall filling below +2.5mPD for TM-CLKL southern and northern landfalls.	TM-CLKL seawall filling	Contractor	TM-EIAO		Y		N/A

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Im	plementa Stages	tion	Status *
	Reference					D	C	0	
6.1	-	a maximum of 30% public fill to be used for reclamation filling below +2.5mPD for TM-CLKL southern landfall	TM-CLKL southern landfall reclamation filling	Contractor	TM-EIAO		Y		N/A
6.1	-	a maximum of 100% public fill to be used for reclamation filling below +2.5mPD for TM-CLKL northern landfall	TM-CLKL northern landfall reclamation filling	Contractor	TM-EIAO		Y		N/A
6.1	-	Use of cage type silt curtains round allgrab dredgers during the HKBCF, HKLR and TM-CLKL southern reclamation works.	All areas dredging works	Contractor	TM-EIAO		Y		N/A
	Figure 1.1 of Annex C	A layer of floating type silt curtain will be applied when dredging and reclamation works are being undertaken at Portion N-a as shown in Figure 1.1 of Annex C of the EM&A Manual.		Contractor	TM-EIAO		Y		N/A
6.1	-	Trailer suction hopper dredgers shall not allow mud to overflow.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1	-	The use of Lean Material Overboard (LMOB) systems shall be prohibited.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1 Figure 6.2b Appendix D6b	Annex A	For other parts of the reclamation works construction of seawalls to be advanced by at least 200m before the main reclamation dredging and filling can commence. It should be noted that the protection by advanced seawall is a dynamic process depending on the progress of the construction activities and the stage when such protection could be realised is illustrated in Figure 6.2b and detailed in Appendices D6b. The part of the works where such measures can be undertaken for the majority of the time includes the following locations: - TM-CLKL northern reclamation; - Reclamation filling for Portion D of HKBCF; Reclamation filling for FSD berth of HKBCF; and	Portion D of HKBCF and HKLR	Contractor	TM-EIAO		Y		N/A
		- Reclamation dredging and filling for Portion 1 of HKLR;							

EIA Reference	Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imj	plementa Stages	tion	Status *
	Reference					D	С	0	
6.1	-	The filling material for the other parts of the works are the same as Sequence A;	All other areas/backfilling works	Contractor	TM-EIAO		Y		N/A
6.1	5.7	Cage type silt curtain (with steel enclosure) shall be used for grab dredgers working in the site of HKBCF and TM- CLKL southern reclamation. Cage type silt curtains will be applied round all grab dredgers at other works area.	grab dredging	Contractor	TM-EIAO		Y		N/A
6.1	Annex A	A layer of floating type silt curtain will be applied around all works as defined in Appendix D6b.	All areas/ through out marine works	Contractor	TM-EIAO		Y		N/A
6.1	-	TM-CLKL northern landfall: - Reclamation filling shall not proceed until at least 200m section of leading seawall at both the east and west sides of the reclamation are formed above +2.5 mPD, except for 100m gaps for marine access;	All areas/ through out marine works	Contractor	TM-EIAO		Y		N/A
General Marine W	orks	•	8		•				
6.1	-	Use of TBM for the construction of the submarine tunnel.	Tunnel works / Construction phase	Contractor	TM-EIAO		Y		N/A
6.1	-	Export dredged spoils from NWWCZ.	All areas as much as possible / dredging activities	Contractor	DASO Permit conditions		Y		N/A
6.1	-	Where public fill is proposed for filling below +2.5mPD, the fine content in the public fill will be controlled to 25%	All areas/ backfilling works	Contractor	TM-EIAO		Y		N/A
6.1	-	Where sand fill is proposed for filling below +2.5mPD, the fine content in the sand fill will be controlled to 5%.	All areas/ backfilling works	Contractor	TM-EIAO		Y		N/A
6.1	-	Mechanical grabs shall be designed and maintained to avoid spillage and should seal tightly while being lifted.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1	-	Barges and hopper dredgers shall have tight fitting seals to their bottom openings to prevent leakage of material.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imj	olementa Stages	tion	Status *
	Reference					D	С	0	
6.1	-	Any pipe leakages shall be repaired quickly. Plant should not be operated with leaking pipes.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1	-	Loading of barges and hoppers shall be controlled to prevent splashing of dredged material to the surrounding water. Barges or hoppers shall not be filled to a level which will cause overflow of materials or pollution of water during loading or transportation.	construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1	-	Excess material shall be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1	-	Adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action;	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1	-	All vessels shall be sized such that adequate clearance is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash.	construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1	-	The works shall not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and adjacent to the works site.	. 0	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		N/A
6.1	5.2	Silt curtain shall have proved effectiveness from the producer and shall be fully maintained throughout the works by the contractor.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A

EIA Reference	EM&A Manual Reference		Location/ Timing	Implementation Agent	Relevant Standard or Requirement		plementa Stages	Status *	
						D	C	0	
6.1	-	The daily maximum production rates shall not exceed those assumed in the water quality assessment.	construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	The dredging and filling works shall be scheduled to spread the works evenly over a working day.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
Land Works									
6.1	-	Wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Sewage effluent and discharges from on- site kitchen facilities shall be directed to Government sewer in accordance with the requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided.	construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm.	, 0	Contractor	TM-EIAO		Y		N/A
6.1	-	Temporary access roads should be surfaced with crushed stone or gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.		Contractor	TM-EIAO		Y		N/A
6.1	-	Measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Open stockpiles of construction materials (e.g. aggregates and sand) on site should be covered with tarpaulin or similar fabric during rainstorms.		Contractor	TM-EIAO		Y		N/A

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imj	olementa Stages	tion	Status *
	Reference					D	C	0	
6.1	5.8	Manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers.	construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	. 0	Contractor	TM-EIAO		Y		N/A
6.1	-	All vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit.	construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Wheel wash overflow shall be directed to silt removal facilities before being discharged to the storm drain.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for off site disposal.	construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	The Contractor shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately.		Contractor	TM-EIAO		Y		N/A
6.1	-	Waste oil should be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance.	All areas/ throughout construction period	Contractor	TM-EIAO Waste Disposal Ordinance		Y		N/A

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation	Relevant Standard or Requirement	Imj	plementa	tion	Status *
	Reference			Agent	or Kequirement	D	Stages C	0	-
6.1	-	All fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank.	construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Surface run-off from bunded areas should pass through oil/grease traps prior to discharge to the stormwater system.	construction period	Contractor	TM-EIAO		Y		N/A
6.1	-	Roadside gullies to trap silt and grit shall be provided prior to discharging the stormwater into the marine environment. The sumps will be maintained and cleaned at regular intervals.	Roadside/design and operation	Design Consultant/ Contractor	TM-EIAO	Y		Y	N/A
6.1	Section 5	All construction works shall be subject to routine audit to ensure implementation of all EIA recommendations and good working practice.	All areas/ throughout construction period	Contractor	EM&A Manual		Y		N/A
Water Quality Mor	iitoring								
6.1	Section 5	Water quality monitoring shall be undertaken for suspended solids, turbidity, and dissolved oxygen. Nutrients and metal parameters shall also be measured for Mf sediment operations (only HKBCF and HKLR required handling of Mf sediment) during baseline, backfilling and post construction period. One year operation phase water quality monitoring at designated stations.	as defined in EM&A Manual, Section 5/ Before, through-out marine construction period, post construction and monthly	Contractor	EM&A Manual		Y	Y	Operational phase water quality monitoring commenced in June 2020 and completed in May 2021.
ECOLOGY 8.14	6.3	Specification for and implement pre, during and post construction dolphin abundance monitoring.	All Areas/Detailed Design/ during construction works/post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	✓
8.14	6.3,6.5	Specification and implementation of 250m dolphin exclusion zone.	All dredging and reclamation areas/Detailed Design/during all reclamation and dredging works	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
8.15	6.3, 6.5	Specification and deployment of an artificial reef of an area of 3,600m2 in an area where fishing activities are prohibited.	activities/Detailed Design/towards end of construction period	TM-CLKL/ HKBCF Design Consultant/TM- CLKL/ HKBCF Contractor	TMEIA	Y		Y	N/A. To be implemented by AFCD.
8.14	6.3, 6.5	Specification and implementation of marine vessel control specifications	All areas/Detailed Design/during construction works	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
8.14	6.3, 6.5	Design and implementation of acoustic decoupling methods for dredging and reclamation works		Design Consultant/ Contractor	TMEIA	Y	Y		N/A

Legend: D=Design, C=Construction, O=Operation

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Im	plementa Stages	tion	Status *
	Reference			8		D	C	0	
8.15	6.3, 6.4	Pre-construction phase survey and coral translocation	Detailed Design/Prior to construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
8.15	6.5	Audit coral translocation success	Post translocation	Contractor	TMEIA		Y		N/A
7.13	6.5	The loss of habitat shall be supplemented by enhancement planting in accordance with the landscape mitigation schedule.	All areas / As soon as accessible	Contractor	TMEIA		Y		N/A
7.13	6.5	Spoil heaps shall be covered at all times.	All areas / Throughout construction period	Contractor	TMEIA		Y		N/A
7.13	6.5	Avoid damage and disturbance to the remaining and surrounding natural habitat	All areas / Throughout construction period	Contractor	TMEIA		Y		N/A
7.13	6.5	Placement of equipment in designated areas within the existing disturbed land	All areas / Throughout construction period	Contractor	TMEIA		Y		N/A
7.13	6.5	Disturbed areas to be reinstated immediately after completion of the works.	All areas / Throughout construction period	Contractor	TMEIA		Y		N/A
7.13	6.5	Construction activities should be restricted to the proposed works boundary.	All areas / Throughout construction period	Contractor	TMEIA		Y		N/A
LANDSCAPE A	AND VISUA	L							
10.9	7.6	The colour and shape of the toll control buildings, ventilation building and administration building shall adopt a design which could blend it into the vicinity elements, and the details will be developed in detailed design stage (DM2)	All areas/detailed design	Design Consultant	TMEIA	Y			N/A
10.9	7.6	Aesthetic design of the viaduct, retaining wall and other structures will be developed under ACABAS submission (DM5)	All areas/detailed design	Design Consultant	TMEIA	Y			N/A
10.9	7.6	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works (CM5)	All areas/detailed design/ during construction/post construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Control night-time lighting and glare by hooding all lights (CM6)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Ensure no run-off into water body adjacent to the Project Area (CM7)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (CM8)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Aesthetically pleasing design (visually unobtrusive and non-reflective) as regard to the form, material and finishes shall be incorporated to all buildings, engineering structures and associated infrastructure facilities (OM5)	All areas/detailed design/ during construction / during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (OM6)	All areas/detailed design/ during construction / during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
<b>WASTE</b> 12.6		The Contractor shall identify a coordinator for the management of waste.	Contract mobilisation	Contractor	TMEIA		Y		N/A

Legend: D=Design, C=Construction, O=Operation

EIA Reference	Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp	Implementation Stages		Status *
	Reference					D	С	0	
12.6		The Contractor shall prepare and implement a Waste Management Plan which specifies procedures such as a ticketing system, to facilitate tracking of loads and to ensure that illegal disposal of wastes does not occur, and protocols for the maintenance of records of the quantities of wastes generated, recycled and disposed. A recording system for the amount of waste generated, recycled and disposed (locations) should be established.		Contractor	TMEIA, Works Branch Technical Circular No. 5/99 for the Trip-ticket System for Disposal of Construction and Demolition Material		Y		N/A

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp	olementa Stages	tion	Status *
	Reference			-	_	D	Č	0	
12.6		The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges.	Contract mobilisation	Contractor	TMEIA, Land (Miscellaneous Provisions) Ordinance (Cap 28); Waste Disposal Ordinance (Cap 354); Dumping at Sea Ordinance (Cap 466); Water Pollution Control Ordinance.		Y		N/A
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedures including waste reduction, reuse and recycling.		Contractor	TMEIA		Y		N/A
12.6	8.1	The extent of cutting operation should be optimised where possible. Earth retaining structures and bored pile walls should be proposed to minimise the extent of cutting.		Contractor	TMEIA		Y		N/A
12.6	8.1	The surplus surcharge should be transferred to a fill bank	Reclamation areas / after surcharge works	Contractor	TMEIA		Y		N/A
12.6	8.1	Rock armour from the existing seawall should be reused on the new sloping seawall as far as possible	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	The site and surroundings shall be kept tidy and litter free.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	No waste shall be burnt on site.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	Provisions to be made in contract documents to allow and promote the use of recycled aggregates where appropriate.	Detailed Design	Design Consultant	TMEIA	Y			N/A
12.6	8.1	The Contractor shall be prohibited from disposing of C&D materials at any sensitive locations. The Contractor should propose the final disposal sites in the EMP and WMP for approval before implementation.	construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	Stockpiled material shall be covered by tarpaulin and /or watered as appropriate to prevent windblown dust/ surface run off.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	Excavated material in trucks shall be covered by tarpaulins to reduce the potential for spillage and dust generation.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	Wheel washing facilities shall be used by all trucks leaving the site to prevent transfer of mud onto public roads.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A

Legend: D=Design, C=Construction, O=Operation

EIA Reference	EM&A	Environmental Protection Measures	Location/ Timing	Implementation	Relevant Standard	Imj	plementa	tion	Status *
	Manual Reference			Agent	or Requirement	D	Stages C	0	
12.6	8.1	Dredged marine mud shall be disposed of in a gazetted marine disposal ground under the requirements of the Dumping at Seas Ordinance.		Contractor	TMEIA	D	Y	0	N/A
12.6	8.1	Standard formwork or pre-fabrication should be used as far as practicable so as to minimise the C&D materials arising. The use of more durable formwork/plastic facing for construction works should be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should avoid over-ordering and wastage.		Contractor	TMEIA		Y		N/A
12.6	8.1	The Contractor should recycle as many C&D materials (this is a waste section) as possible on-site. The public fill and C&D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials. Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.		Contractor	TMEIA		Y		N/A
12.6	8.1	All falsework will be steel instead of wood.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	Chemical waste producers should register with the EPD. Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows: <i>f</i> suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed; <i>f</i> Having a capacity of <450L unless the specifications have been approved by the EPD; and w Chinese according to the instructions prescribed in Schedule 2 of the Regulations. <i>f</i> Clearly labelled and used solely for the storage of chemical wastes; <i>f</i> Enclosed with at least 3 sides; <i>f</i> Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest; <i>f</i> Adequate ventilation;		Contractor	TMEIA		Y		N/A

Legend: D=Design, C=Construction, O=Operation

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imj	olementa Stages	tion	Status *
	Reference				or nequirement	D	C	0	
		<i>f</i> Sufficiently covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and <i>f</i> Incompatible materials are adequately separated.							
12.6	8.1	Waste oils, chemicals or solvents shall not be disposed of to drain,	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	Adequate numbers of portable toilets should be provided for on- site workers. Portable toilets should be maintained in reasonable states, which will not deter the workers from utilising them.		Contractor	TMEIA		Y		N/A
12.6	8.1	Night soil should be regularly collected by licensed collectors.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	General refuse arising on-site should be stored in enclosed bins or compaction units separately from C&D and chemical wastes. Sufficient dustbins shall be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station. Burning of refuse on construction sites is prohibited.	construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	All waste containers shall be in a secure area on hardstanding;	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including waste reduction, reuse and recycling.	All areas / throughout	Contractor	TMEIA		Y		N/A
12.6	8.1	Office wastes can be reduced by recycling of paper if such volume is sufficiently large to warrant collection. Participation in a local collection scheme by the Contractor should be advocated. Waste separation facilities for paper, aluminium cans, plastic bottles, etc should be provided on-site.	construction period	Contractor	TMEIA		Y		N/A
12.6	Section 8	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.		Contractor	EM&A Manual		Y		N/A
CULTURAL HE	Section 9	EM&A in the form of audit of the mitigation measures	All areas / throughout construction period	Highways Department	EIAO-TM		Y		N/A

\* Remarks:

✓ Compliance of Mitigation Measures

<> Compliance of Mitigation but need improvement

x Non-compliance of Mitigation Measures

Legend: D=Design, C=Construction, O=Operation

EIA Re	eference	EM&A	Environmental Protection Measures	Location/ Timing	Implementation	<b>Relevant Standard</b>	Imp	lementa	tion	Status *
		Manual			Agent	or Requirement		Stages		
	1	Reference					D	С	0	
	No	on-complianc	e of Mitigation Measures but rectified by Contractor							
Δ	De	eficiency of M	litigation Measures but rectified by Contractor							

N/A Not Applicable in Reporting Period

Legend: D=Design, C=Construction, O=Operation

Appendix D

EM&A Monitoring Schedules

## HY/2012/08 - Tuen Mun - Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section Operational Phase Dolphin Monitoring Survey Monitoring Schedule - August 2021

Quadau	Manalas	Tuesday	Mante endere	Thursday	Friday	Octorday
Sunday 01-Aug	Monday 02-Aug	Tuesday 03-Aug	Wednesday 04-Aug	Thursday 05-Aug	Friday 06-Aug	Saturday 07-Aug
01-Aug		Operational Phase Dolphin Monitoring		Operational Phase Dolphin Monitoring	00-749	<u>Ur-Aug</u>
08-Aug	09-Aug	10-Aug	11-Aug	12-Aug	13-Aug	14-Aug
	Operational Phase Dolphin Monitoring					
15-Aug	16-Aug	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug
22-Aug	23-Aug		25-Aug	26-Aug	27-Aug	28-Aug
		Operational Phase Dolphin Monitoring				
29-Aug	30-Aug	31-Aug				

Appendix E

Operational Phase Dolphin Monitoring Survey

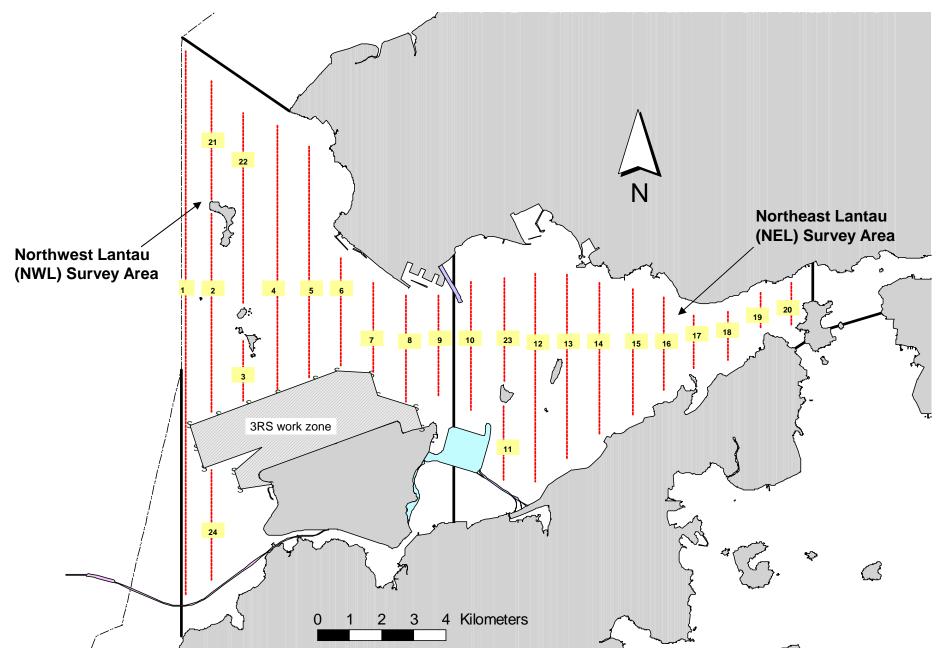


Figure 1. Transect Line Layout in Northwest and Northeast Lantau Survey Areas

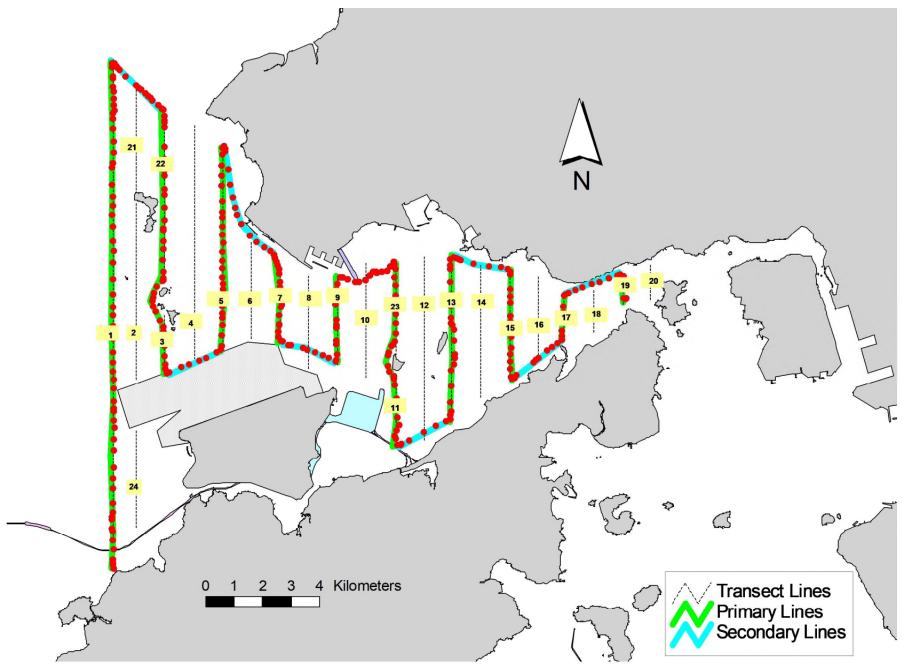


Figure 2. Survey Route on August 3rd, 2021

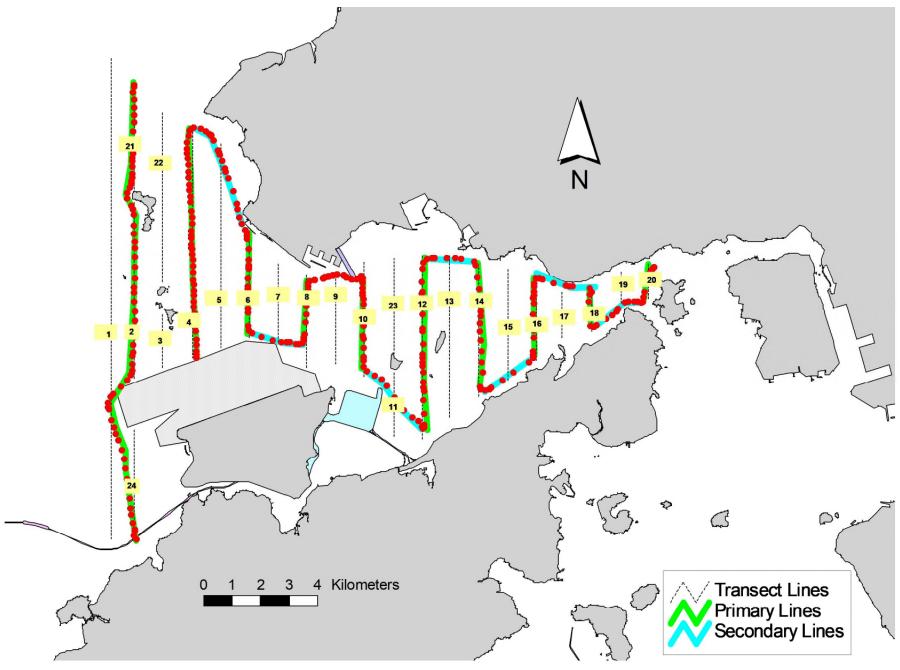


Figure 3. Survey Route on August 5th, 2021

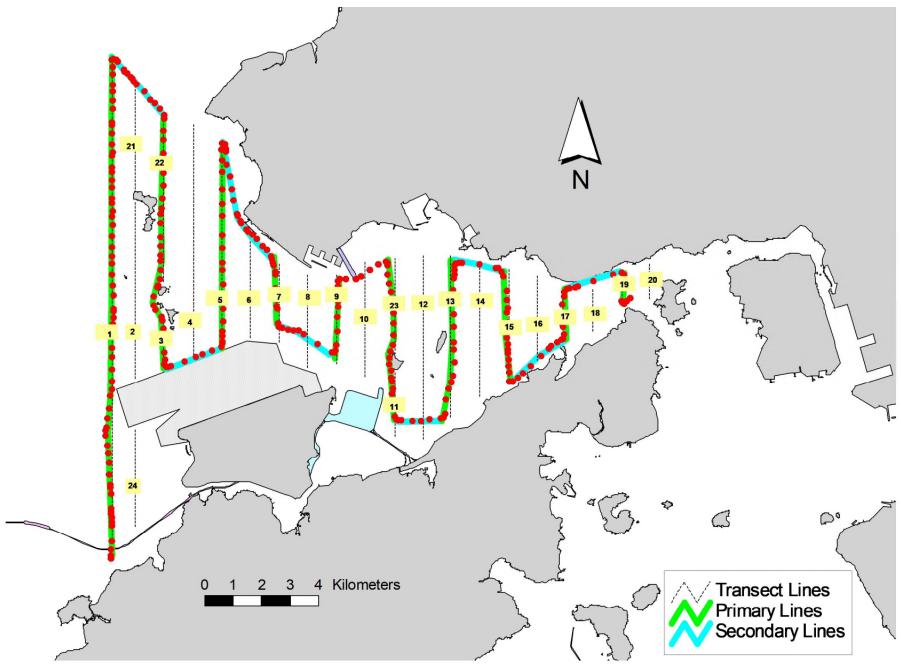


Figure 5. Survey Route on August 9th, 2021

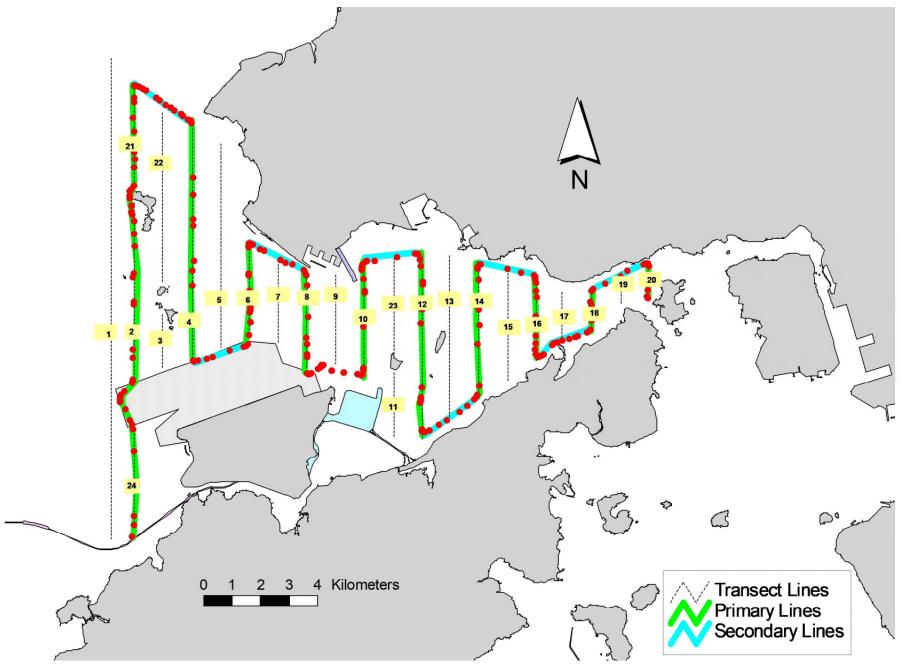


Figure 4. Survey Route on August 24th, 2021

## Appendix I. TMCLKL Survey Effort Database (August 2021)

(Abbreviations: BEAU = Beaufort Sea State; P = Primary Line Effort; S = Secondary Line Effort)

DATE	AREA	BEAU	EFFORT	SEASON	VESSEL	TYPE	P/S
3-Aug-21	NW LANTAU	1	1.10	SUMMER	STANDARD36826	TMCLKL	Р
3-Aug-21	NW LANTAU	2	13.28	SUMMER	STANDARD36826	TMCLKL	Р
3-Aug-21	NW LANTAU	3	23.12	SUMMER	STANDARD36826	TMCLKL	Р
3-Aug-21	NW LANTAU	2	9.30	SUMMER	STANDARD36826	TMCLKL	S
3-Aug-21	NW LANTAU	3	2.60	SUMMER	STANDARD36826	TMCLKL	S
3-Aug-21	NE LANTAU	1	1.20	SUMMER	STANDARD36826	TMCLKL	Р
3-Aug-21	NE LANTAU	2	13.39	SUMMER	STANDARD36826	TMCLKL	Р
3-Aug-21	NE LANTAU	3	2.60	SUMMER	STANDARD36826	TMCLKL	Р
3-Aug-21	NE LANTAU	1	1.40	SUMMER	STANDARD36826	TMCLKL	S
3-Aug-21	NE LANTAU	2	7.31	SUMMER	STANDARD36826	TMCLKL	S
5-Aug-21	NW LANTAU	2	2.90	SUMMER	STANDARD138716	TMCLKL	Р
5-Aug-21	NW LANTAU	3	27.11	SUMMER	STANDARD138716	TMCLKL	Р
5-Aug-21	NW LANTAU	2	1.20	SUMMER	STANDARD138716	TMCLKL	S
5-Aug-21	NW LANTAU	3	4.09	SUMMER	STANDARD138716	TMCLKL	S
5-Aug-21	NE LANTAU	2	7.89	SUMMER	STANDARD138716	TMCLKL	Р
5-Aug-21	NE LANTAU	3	10.89	SUMMER	STANDARD138716	TMCLKL	Р
5-Aug-21	NE LANTAU	2	2.10	SUMMER	STANDARD138716	TMCLKL	S
5-Aug-21	NE LANTAU	3	8.42	SUMMER	STANDARD138716	TMCLKL	S
9-Aug-21	NW LANTAU	2	16.60	SUMMER	STANDARD138716	TMCLKL	Р
9-Aug-21	NW LANTAU	3	18.90	SUMMER	STANDARD138716	TMCLKL	Р
9-Aug-21	NW LANTAU	1	2.20	SUMMER	STANDARD138716	TMCLKL	S
9-Aug-21	NW LANTAU	2	6.30	SUMMER	STANDARD138716	TMCLKL	S
9-Aug-21	NW LANTAU	3	3.90	SUMMER	STANDARD138716	TMCLKL	S
9-Aug-21	NE LANTAU	2	17.30	SUMMER	STANDARD138716	TMCLKL	Р
9-Aug-21	NE LANTAU	2	6.30	SUMMER	STANDARD138716	TMCLKL	S
9-Aug-21	NE LANTAU	3	1.30	SUMMER	STANDARD138716	TMCLKL	S
24-Aug-21	NW LANTAU	2	28.93	SUMMER	STANDARD36826	TMCLKL	Р
24-Aug-21	NW LANTAU	2	7.97	SUMMER	STANDARD36826	TMCLKL	S
24-Aug-21	NE LANTAU	1	5.95	SUMMER	STANDARD36826	TMCLKL	Р
24-Aug-21	NE LANTAU	2	10.48	SUMMER	STANDARD36826	TMCLKL	Р
24-Aug-21	NE LANTAU	3	2.70	SUMMER	STANDARD36826	TMCLKL	Р
24-Aug-21	NE LANTAU	1	3.27	SUMMER	STANDARD36826	TMCLKL	S
24-Aug-21	NE LANTAU	2	7.10	SUMMER	STANDARD36826	TMCLKL	S
24-Aug-21	NE LANTAU	3	0.30	SUMMER	STANDARD36826	TMCLKL	S

Appendix F

Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

## Table F1Cumulative Statistics on Exceedances

Parameters	Level of Exceedance	Total No. recorded in this reporting month	Total No. recorded since Contract commencement
1-hr TSP	Action	0	122
	Limit	0	15
24-hr TSP	Action	0	12
	Limit	0	4
Water Quality	Action	0	167
	Limit	0	19
Impact Dolphin	Action	0	11
Monitoring	Limit	0	19

# Table F2Cumulative Statistics on Complaints, Notifications of Summons and<br/>Successful Prosecutions

<b>Reporting Period</b>			
	Complaints	Notifications of	Successful
	_	Summons	Prosecutions
This Reporting Month (August 2021)	0	0	0
Total No. received since Contract commencement	17	1	0

ENVIRONMENTAL RESOURCES MANAGEMENT

Appendix G

Waste Flow Table



## Monthly Summary Waste Flow Table

# Contract No. / Works Order No.: <u>HY/2012/08</u>

Name of Department:HyDMonthly Summary Waste Flow Table forAugust 2021month] (All quantities shall be rounded off to 3 decimal places.)

[to be submitted not later than the 15<sup>th</sup> day of each month following reporting

	I	Monthly Break-down of <u>Inert</u> Construct	ion & Demolition Materia	als (i.e. Public Fill Materials	)
Month	(a)=(b)+(c)+(d)+(e) Total Quantity Generated	(b) Hard Rock and Large Broken Concrete	(c) Reused in the Contract	(d) Reused in other Projects	(e) Disposed of as Public Fill
	(in '000 ton)	(in '000 ton)	(in '000 ton)	(in '000 ton)	(in '000 ton)
Sub-total	3205.825	0.000	336.902	889.467	1979.479
Jan-2021	1.031	0.000	0.000	0.000	1.031
Feb-2021	0.210	0.000	0.000	0.000	0.210
Mar-2021	0.409	0.000	0.000	0.000	0.409
Apr-2021	0.008	0.000	0.000	0.000	0.008
May-2021	0.000	0.000	0.000	0.000	0.000
Jun-2021	0.031	0.000	0.000	0.000	0.031
Half Year Sub-total	1.689	0.000	0.000	0.000	1.689
Jul-2021	0.039	0.000	0.000	0.000	0.039
Aug-2021	0.017	0.000	0.000	0.000	0.017
Sep-2021					
Oct-2021					
Nov-2021					
Dec-2021					
Project Total Quantities	3207.57	0.000	336.902	889.467	1981.224



	Actual Quantities of <u>Non-inert</u> Construction Waste Generated Monthly								
Month	Metals		Paper/ cardboard packaging		Plastics (see Note 3)		Chemical Waste		Others, e.g. General Refuse disposed at Landfill
	(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000ton)
	generated	recycled	generated	recycled	generated	recycled	generated	Disposed	generated
Sub-total	9919.11	9919.11	18.28	18.28	16.84	16.84	93.807	93.807	28.243
Jan-2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.071
Feb-2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.011
Mar-2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.034
Apr-2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.068
May-2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.028
Jun-2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.033
Half Year Sub-total	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.245
Jul-2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.009
Aug-2021	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.007
Sep-2021									
Oct-2021									
Nov-2021									
Dec-2021									
Project Total Quantities	9919.11	9919.11	18.28	18.28	16.84	16.84	93.807	93.807	28.504



Forecast of Total Quantities of Construction and Demolition Materials to be Generated from the Contract*							
Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed of as Public Fill			
(in '000 ton)	(in '000 ton)	(in '000 ton)	(in '000 ton)	(in '000 ton)			
3200.000	0.000	350.000	1000.000	2000.000			

Forecast of Total Quantities of Construction and Demolition Materials to be Generated from the Contract*							
Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	General Refuse disposed of at Landfill			
(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 ton)			
10000.00	20.00	18.00	120.00	30.000			

Notes:

(1) The performance targets are given in the **ER Appendix 8J Clause 14** and the EM & A Manual(s).

(2) The waste flow table shall also include C&D materials to be imported for use at the Site.

(3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.

(4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m<sup>3</sup>. (**ER Part 8 Clause 8.8.5** (d) (ii) refers).
