

NENT NDAs Study Implementation Programme and Phasing - Gantt Chart Programme

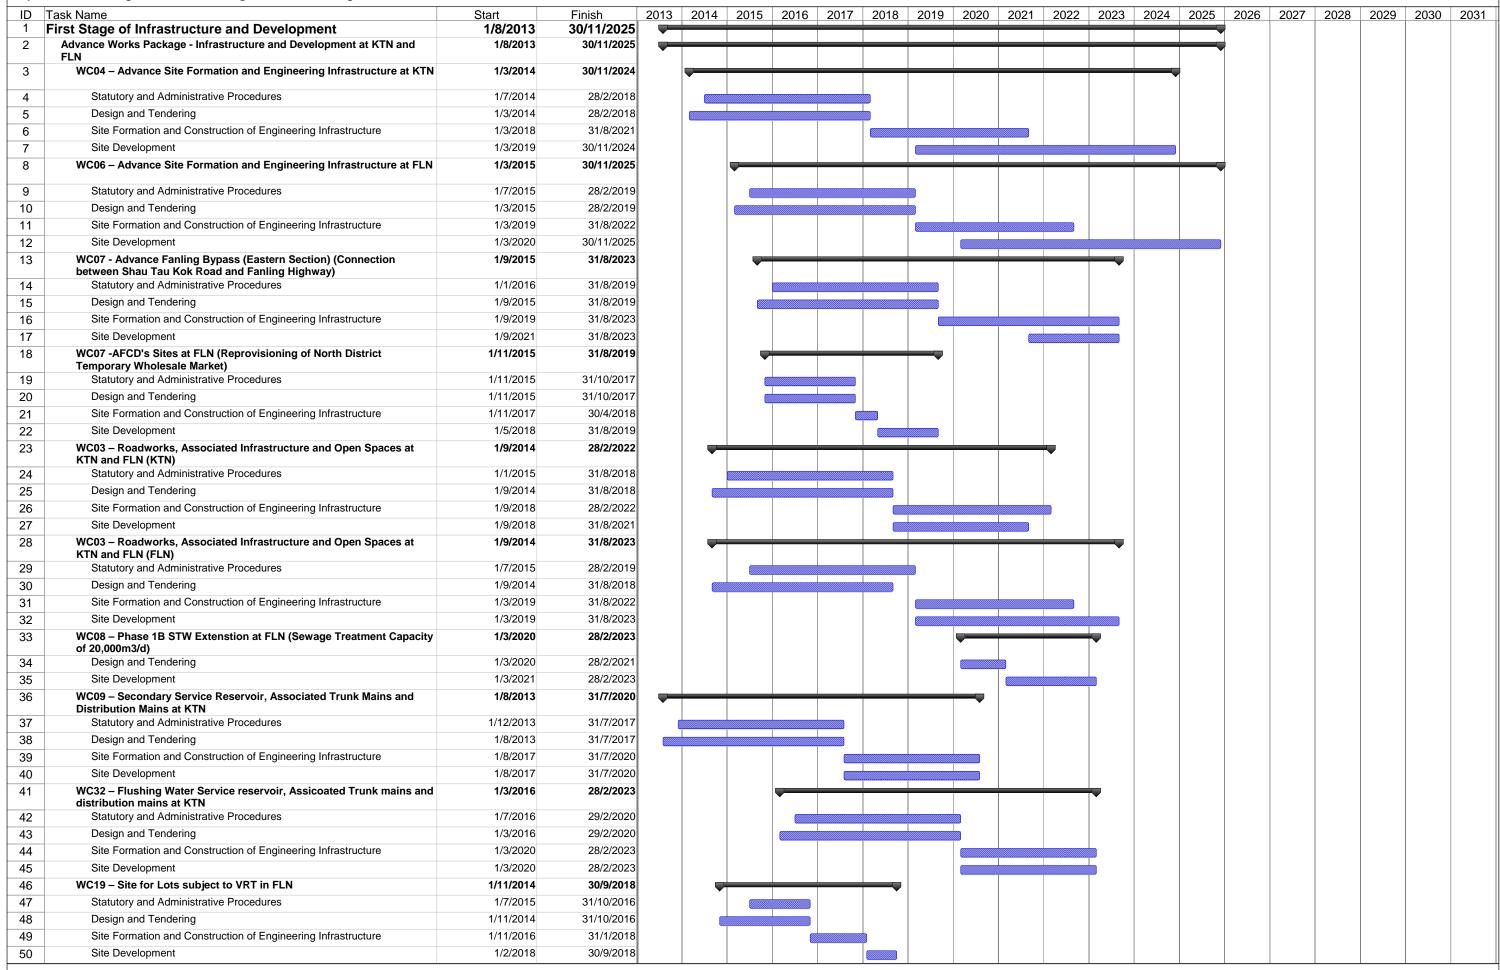

NENT NDAs Study Implementation Programme and Phasing - Gantt Chart Programme

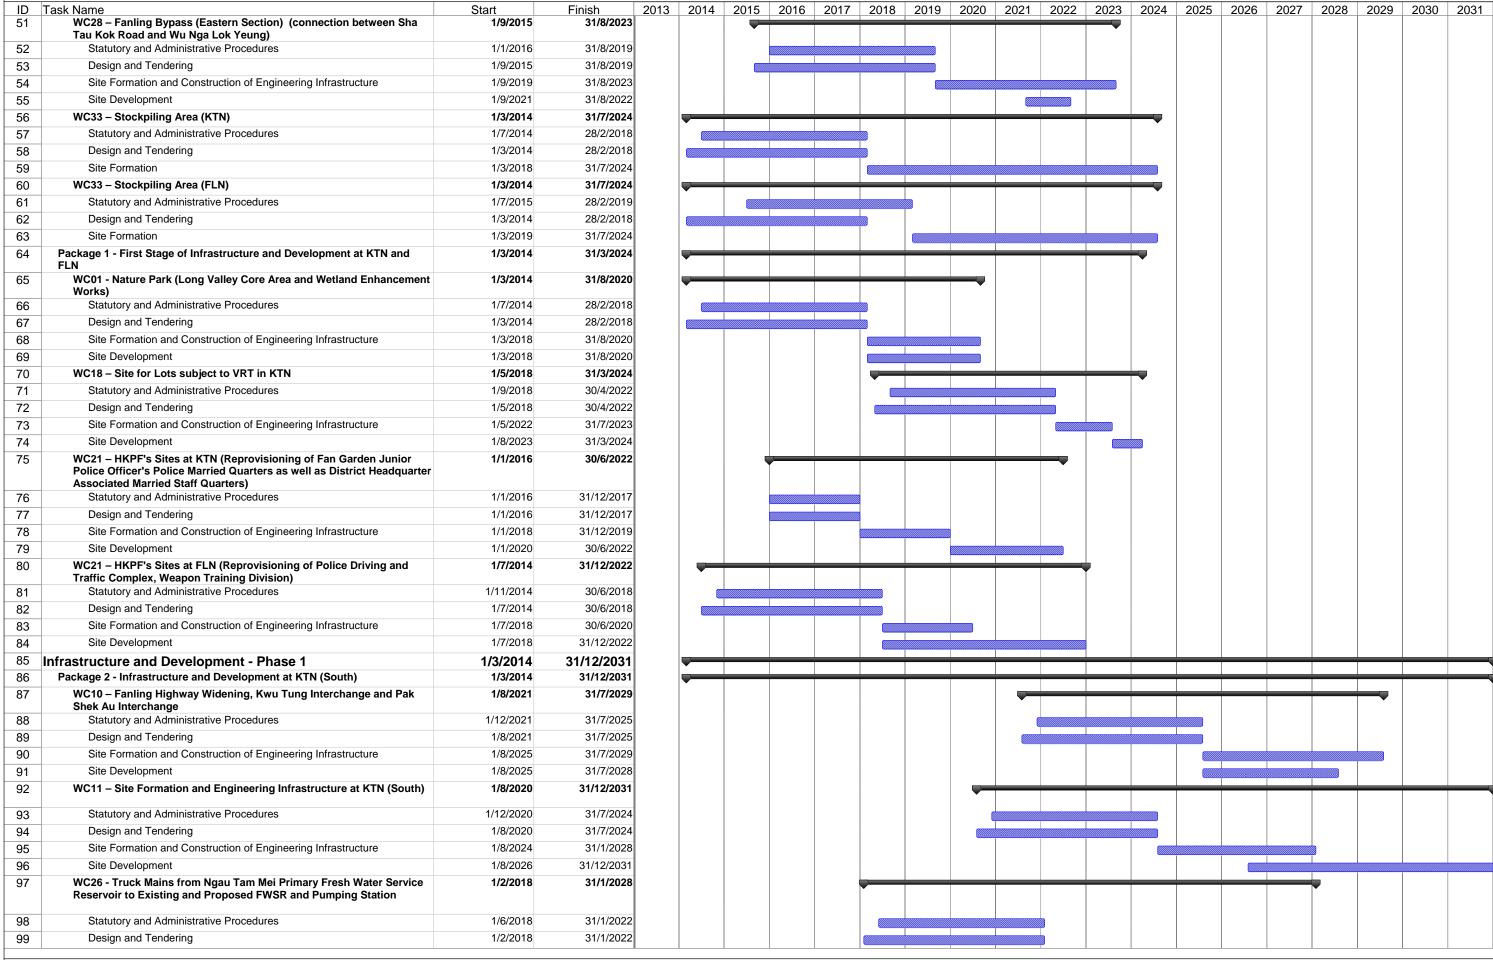

NENT NDAs Study Implementation Programme and Phasing - Gantt Chart Programme ID Task Name 2013 | 2014 | 2015 | 2016 | 2017 | 2018 | 2019 | 2020 | 2021 | 2022 | 2023 | 2024 | 2025 | 2026 | 2027 | 2028 2029 2030 2031 Start Finish Site Formation and Construction of Engineering Infrastructure 1/2/2022 31/1/2028 100 101 WC31 - Plant for District Colling System at KLN 1/3/2014 28/2/2023 102 Statutory and Administrative Procedures 1/7/2014 28/2/2018 103 Design and Tendering 1/3/2014 28/2/2018 Site Formation and Construction of Engineering Infrastructure 1/3/2018 28/2/2021 104 1/3/2020 28/2/2023 105 Site Development 106 Package 3 - Infrastructure and Development at KTN (North) 1/1/2016 31/12/2031 107 WC12 - Site Formation and Engineering Infrastructure at KTN (North) 1/8/2020 31/12/2031 108 Statutory and Administrative Procedures 1/12/2020 31/7/2024 1/8/2020 31/7/2024 109 Design and Tendering 110 Site Formation and Construction of Engineering Infrastructure 1/8/2024 31/1/2028 Site Development 1/8/2026 31/12/2031 111 112 WC21 - HKPF's Sites at KTN (District Headquarters and Divisional 1/8/2022 31/1/2029 Police Station) 113 Design and Tendering 1/8/2022 31/7/2024 Site Formation and Construction of Engineering Infrastructure 1/8/2024 31/7/2026 114 1/8/2026 31/1/2029 115 Site Development 116 WC29 - Reprovisioning Sites for community Sports 1/1/2016 31/12/2023 Statutory and Administrative Procedures 1/5/2016 31/12/2019 117 1/1/2016 31/12/2019 118 Design and Tendering 119 Site Formation and Construction of Engineering Infrastructure 1/1/2020 31/12/2021 1/1/2022 120 Site Development 31/12/2023 121 Infrastructure and Development - Phase 2 1/2/2017 31/12/2031 122 Package 4 - Remaining Infrastructure and Development at FLN (East) 1/2/2017 31/12/2031 123 WC13 - Secondary Services Reservoir, Associated Trunk Mains and 1/2/2017 31/1/2025 **Distribution Mains at FLN** 1/6/2017 31/1/2021 124 Statutory and Administrative Procedures Design and Tendering 1/2/2017 31/1/2021 125 1/2/2021 126 Site Formation and Construction of Engineering Infrastructure 31/1/2025 127 1/2/2021 Site Development 31/1/2025 128 WC14 - Fanling Bypass (Western Section) (Connection between Man 1/8/2021 31/7/2029 Kam To Road and Sha Tau Kok Road) and Po Shek Wu Interchange Improvement 1/12/2021 31/7/2025 129 Statutory and Administrative Procedures 130 Design and Tendering 1/8/2021 31/7/2025 31/7/2029 131 Site Formation and Construction of Engineering Infrastructure 1/8/2025 132 Site Development 1/8/2027 31/7/2028 31/12/2031 133 WC15 -Remaining Site Formation and Engineering Infrastructure at 1/8/2020 Statutory and Administrative Procedures 1/12/2020 31/7/2024 134 135 1/8/2020 31/7/2024 Design and Tendering 136 Site Formation and Construction of Engineering Infrastructure 1/8/2024 31/1/2028 137 Site Development 1/8/2026 31/12/2031 31/12/2031 138 Package 5 - Remaining Infrastructure and Development at FLN (West) 1/11/2018 139 WC08 - Phase 2 STW Extenstion at FLN (Sewage Treatment Capacity 1/11/2018 31/1/2028 of 110,000m3/d) 1/3/2019 31/10/2022 140 Statutory and Administrative Procedures 31/10/2022 141 Design and Tendering 1/11/2018 142 Site Formation and Construction of Engineering Infrastructure 1/11/2022 31/1/2028 Site Development 1/11/2022 31/1/2028 143 144 WC22 - Remaining Site Formation and Engineering Infrastructure at 1/8/2020 31/12/2031 FLN (West) 145 Statutory and Administrative Procedures 1/12/2020 31/7/2024 1/8/2020 31/7/2024 146 Design and Tendering 147 Site Formation and Construction of Engineering Infrastructure 1/8/2024 31/1/2028

Site Development

148

1/8/2026

31/12/2031
