



Lam Geotechnics Limited

Contract No. HK/2015/01
Wanchai Development Phase II and Central Wanchai Bypass
- Sampling, Field Measurement and Testing Works (Stage 3)
Quarterly EM&A Report (March 2017 to May 2017)

CONTRACT NO: HK/2015/01

**WANCHAI DEVELOPMENT PHASE II AND CENTRAL
WANCHAI BYPASS
SAMPLING, FIELD MEASUREMENT AND TESTING WORK
(STAGE 3)**

**ENVIRONMENTAL PERMIT NO. EP-364/2009/E,
FURTHER ENVIRONMENTAL PERMIT NOS. FEP-01/364/2009,
FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A, FEP-
07/364/2009/D, FEP-09/364/2009/B, FEP-10/364/2009/B AND
FEP-11/364/2009/B, FEP-12/364/2009/D**

**QUARTERLY ENVIRONMENTAL MONITORING
AND AUDIT REPORT**

- MARCH 2017 TO MAY 2017 -

CLIENTS:

**Civil Engineering and Development
Department**

and

Highways Department

PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point
181-185 Gloucester Road,
Wanchai, H.K.

Telephone: (852) 2882-3939

Facsimile: (852) 2882-3331

E-mail: info@lamenviro.com

Website: <http://www.lamenviro.com>

CHECKED BY:

Raymond Dai
Environmental Team Leader

DATE:

28 June 2017

Ref.: AACWBIECEM00_0_9493L.17

29 June 2017

AECOM Asia Company Limited
11/F Tower 2 Grand Central Plaza
138 Shatin Rural Committee Road
Shatin New Territories
Hong Kong

By Post and Fax (2691 2649)

Attention: Mr. Conrad Ng

Dear Mr. Ng,

**Re: Contract No. HK/2015/01
Wan Chai Development Phase II - Central-Wan Chai Bypass
Sampling, Field Measurement and Testing Works (Stage 3)**

Quarterly Environmental Monitoring and Audit Report (March 2017 to May 2017) for EP-364/2009/E

Reference is made to the Environmental Team's submission of the captioned Quarterly Environmental Monitoring and Audit (EM&A) Report received by e-mail on 28 June 2017 for our review and comment.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission.

Thank you for your attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



David Yeung
Independent Environmental Checker

c.c.	CEDD	Attn: Mr. Stephen Lo	by fax: 2577 5040
	Lam	Attn: Mr. Raymond Dai	by fax: 2882 3331
	AECOM	Attn: Mr. Francis Leong / Stephen Lai	by fax: 2691 2649

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00_0_9493L.17.docx

TABLE OF CONTENTS

1. INTRODUCTION.....	16
1.1 Scope of the Report	16
1.2 Structure of the Report	16
2. PROJECT BACKGROUND.....	17
2.1 Background	17
2.2 Scope of the Project and Site Description.....	17
2.3 Division of the Project Responsibility	18
2.4 Project Organization and Contact Personnel.....	20
2.5 Principal Work and Activities	22
3. MONITORING REQUIREMENTS	26
3.1. Noise Monitoring.....	26
3.2. Air quality monitoring	28
4. MONITORING RESULTS	31
4.1. Noise Monitoring Results	32
4.2. Real Time Noise Monitoring Results	36
4.3. Air quality monitoring Results	40
4.4. Waste Monitoring Results	46
5. COMPLIANCE AUDIT	51
5.1. Noise Monitoring.....	51
5.2. Air quality monitoring	53
5.3. Real Time Noise Monitoring	55
5.4. Site Audit.....	57
5.5. Review of the Reasons for and the Implications of Non-compliance.....	59
5.6. Summary of action taken in the event of and follow-up on non-compliance	59
6. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION	60
7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS.....	65
8. CONCLUSION.....	66

LIST OF TABLES

Table I	<i>Principal Work Activities for Contract no. HY/2009/18</i>
Table II	<i>Principal Work Activities for Contract no. HK/2009/01</i>
Table III	<i>Principal Work Activities for Contract no. HK/2009/02</i>
Table IV	<i>Principal Work Activities for Contract no. HY/2009/15</i>
Table V	<i>Principal Work Activities for Contract no. HY/2009/19</i>
Table VI	<i>Principal Work Activities for Contract no. HK/2012/08</i>
Table VII	<i>Principal Work Activities for Contract no. HY/2010/08</i>
Table VIII	<i>Principal Work Activities for Contract no. HY/2011/08</i>
Table 2.1	<i>Schedule 2 Designated Projects under this Project</i>
Table 2.2	<i>Details of Individual Contracts under the Project</i>
Table 2.3	<i>Contact Details of Key Personnel</i>
Table 2.4	<i>Principal Work Activities for Contract no. HY/2009/18</i>
Table 2.5	<i>Principal Work Activities for Contract no. HK/2009/01</i>
Table 2.6	<i>Principal Work Activities for Contract no. HK/2009/02</i>
Table 2.7	<i>Principal Work Activities for Contract no. HY/2009/15</i>
Table 2.8	<i>Principal Work Activities for Contract no. HY/2009/19</i>
Table 2.9	<i>Principal Work Activities for Contract no. HK/2012/08</i>
Table 2.10	<i>Principal Work Activities for Contract no. HY/2010/08</i>
Table 2.11	<i>Principal Work Activities for Contract no. HY/2011/08</i>
Table 3.1	<i>Noise Monitoring Stations</i>
Table 3.2	<i>Real Time Noise Monitoring Stations</i>
Table 3.3	<i>Air quality monitoring Stations</i>
Table 4.1	<i>Noise Monitoring Station for Contract no. HY/2009/18</i>
Table 4.2	<i>Noise Monitoring Stations for Contract nos. HK/2009/01 and HK/2009/02</i>
Table 4.3	<i>Noise Monitoring Station for Contract nos. HY/2009/15</i>
Table 4.4	<i>Noise Monitoring Stations for Contract no. HY/2009/19</i>
Table 4.5	<i>Noise Monitoring Stations for Contract no. HY/2010/08</i>
Table 4.6	<i>Noise Monitoring Stations for Contract no. HY/2011/08</i>
Table 4.7	<i>Real Time Noise Monitoring Stations for Contract no. HY/2009/19</i>
Table 4.8	<i>Real Time Noise Monitoring Stations for Contract no. HY/2011/08</i>
Table 4.9	<i>Air quality monitoring Stations for Contract no. HY/2009/18</i>
Table 4.10	<i>Air quality monitoring Stations for Contract no. HK/2009/01</i>
Table 4.11	<i>Air quality monitoring Station for Contract no. HK/2009/02</i>
Table 4.12	<i>Air quality monitoring Station for Contract no. HY/2009/15</i>
Table 4.13	<i>Air quality monitoring Stations for Contract no. HY/2009/19</i>
Table 4.14	<i>Air quality monitoring Stations for Contract no. HK/2012/08</i>
Table 4.15	<i>Air quality monitoring Stations for Contract no. HY/2010/08</i>
Table 4.16	<i>Air quality monitoring Stations for Contract no. HY/2011/08</i>
Table 4.17	<i>Details of Waste Disposal for Contract no. HK/2009/01</i>
Table 4.18	<i>Details of Waste Disposal for Contract no. HK/2009/02</i>
Table 4.19	<i>Details of Waste Disposal for Contract no. HY/2009/18</i>
Table 4.20	<i>Details of Waste Disposal for Contract no. HY/2009/15</i>
Table 4.21	<i>Details of Waste Disposal for Contract no. HY/2009/19</i>
Table 4.22	<i>Details of Waste Disposal for Contract no. HK/2012/08</i>
Table 4.23	<i>Details of Waste Disposal for Contract no. HY/2010/08</i>
Table 4.24	<i>Details of Waste Disposal for Contract no. HY/2011/08</i>
Table 6.1	<i>Cumulative Statistics on Complaints</i>
Table 6.2	<i>Cumulative Statistics on Successful Prosecutions</i>



LIST OF FIGURES

<u>Figure 2.1</u>	Project Layout
<u>Figure 2.2</u>	Project Organization Chart
<u>Figure 3.1</u>	Locations of Environmental Monitoring Stations

LIST OF APPENDICES

<u>Appendix 2.1</u>	Environmental Mitigation Implementation Schedule
<u>Appendix 3.1</u>	Action and Limit Level
<u>Appendix 4.1</u>	Noise Monitoring Results and Graphical Presentations
<u>Appendix 4.2</u>	Real-time Noise Monitoring Results and Graphical Presentations
<u>Appendix 4.3</u>	Air Quality Monitoring Results and Graphical Presentations
<u>Appendix 5.1</u>	Event Action Plans
<u>Appendix 6.1</u>	Complaint Log
<u>Appendix 6.2</u>	Notification of Exceedance
<u>Appendix 8.1</u>	Construction Programme of Individual Contracts

EXECUTIVE SUMMARY

- i. This is the Environmental Monitoring and Audit (EM&A) Quarterly Report – [March 2017 to May 2017](#) specific for Environmental Permit no. EP-364/2009/E, Further Environmental Permit nos. FEP-01/364/2009, FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A, FEP-07/364/2009/D, FEP-09/364/2009/B, FEP-10/364/2009/B AND FEP-11/364/2009/B. The EM&A report is prepared by the Environmental Team (ET) employed under Contract No. HK/2011/07 – Wan Chai Development Phase II and Central Wanchai Bypass – Sampling, Field Measurement and Testing Works (Stage 2). This report presents the environmental monitoring findings and information recorded during the period from [27 February 2017 to 26 May 2017](#). The cut-off date of reporting is at 26th of each reporting quarter.

- ii. In the reporting quarter, the principal work activities of individual contracts are included as follows:

Contract no. HY/2009/18 - Central - Wan Chai Bypass (CWB) - Central Interchange under FEP-05/364/2009

Major construction activities for Contract no. HY/2009/18 have been commenced on 21 April 2011. During this reporting period, the principal work activities for Contract no. HY/2009/18 are summarized as below:

Table I Principal Work Activities for Contract no. HY/2009/18

March 2017	April 2017	May 2017
• Drainage works • Road works • Landscaping works • Maintenance works	• Drainage works • Road works • Landscaping works • Maintenance works	• Drainage works • Road works • Landscaping works • Maintenance works

Contract no. HK/2009/01 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Hong Kong Convention and Exhibition Centre - Tunnel Works under FEP-02/364/2009

Major construction activities for Contract no. HK/2009/01 have been commenced on 25 August 2011. During this reporting period, the principal work activities are summarized as below:

Table II Principal Work Activities for Contract no. HK/2009/01

March 2017	April 2017	May 2017
• Reinstatement of amenity area • Road and Drain works	• Reinstatement of amenity area • Road and Drain works	• Reinstatement of amenity area • Road and Drain works

Contract no. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

Major construction activities for Contract no. HK/2009/02 have been commenced on 26 April 2011. During this reporting period, the principal work activities are summarized as below:

Table III Principal Work Activities for Contract no. HK/2009/02

March 2017	April 2017	May 2017
- Defective works for Star Ferry Pier - Rectification works for cross road ducts - Rectification works for cracks/joints with water leakage inside OHVD cells - Removal works for ELS S1 - Demolition works for Hung Hing Road Flyover abutment - Backfilling works - Temporary wall for construction of Hung Hing Road Flyover - Concreting mass concrete underneath Hung Hing Road Flyover - Delivery of precast concrete seawall block - Cleaning of cross road duct & carrier drain - Rectification works against water leakage and remedial works against concrete defects of the tunnel structure - Waterproofing laying work - Concreting for base slab - Removal of ELS layer S2 & S3 - Tunnel wall structure	- Rectification works for the defects recorded in the inspection for the end of maintenance period of Observation Deck and Staircase ST-01 - Rectification works for cross road ducts - rectification works for cracks/joints with water leakage inside OHVD cells - Backfilling works - Construction of temporary wall for inside tunnel - Blinding layer for Hung Hing Road Flyover - Cleaning of cross road duct & carrier drain - Rectification works against water leakage and remedial works against concrete defects of the tunnel structure - Outstanding works inside tunnel - Concreting for base slab - Removal of ELS layer S2 & S3 - Tunnel wall structure - Concreting for roadside barrier - Erection of scaffolding for construction of OHVD - Concreting for OHVD slab - Erection of scaffolding for construction of top slab	- Rectification works for the defects recorded in the inspection for the end of maintenance period of Observation Deck and Staircase ST-01 - completion of rectification works for cracks/joints with water leakage inside OHVD cells - backfilling works - construction of temporary wall for inside tunnel - blinding layer for Hung Hing Road Flyover - demolition of diaphragm wall for reinstatement of Hung Hing Road approach ramp - cleaning of cross road duct - Rectification works against water leakage and remedial works against concrete defects of the tunnel structure - outstanding works inside tunnel - Tunnel wall structure - Concreting for roadside barrier - Erection of scaffolding for construction of OHVD - Concreting for OHVD slab - Erection of scaffolding for construction of top slab - Tunnel top slab - Rectification work for road

• Concreting for roadside barrier • Erection of scaffolding for construction of OHVD • Excavation works for trial pit for the 132kV HK Electric Cables		defects at Wan Shing Street

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

Major construction activities for Contract no. HY/2009/15 has been commenced on 13 July 2011. During this reporting period, the principal work activities are summarized as below:

Table IV Principal Work Activities for Contract no. HY/2009/15

March 2017	April 2017	May 2017
• Remedial works inside tunnel structure at Mined Tunnel, TS4, TPCWAE and TPCWAW • Reinstatement of drainage pipes and manhole at TPCWAE	• Remedial works inside tunnel structure at Mined Tunnel, TS4, TPCWAE and TPCWAW • Reinstatement work at the PRE Office car park area	• Remedial works inside tunnel structure at Mined Tunnel, TS4, TPCWAE and TPCWAW • Reinstatement work at the PRE Office car park area

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

Major construction activities for Contract no. HY/2009/19 have been commenced on March 2011. During this reporting period, the principal work activities are summarized as below:

Table V Principal Work Activities for Contract no. HY/2009/19

March 2017	April 2017	May 2017
• Approach ramp sheet piling, pre-bored piling and top soil removal works • Hing Fat Street modification works • Bridge Demolition / Construction • Hotel Carpark Reinstatement • Bridge E noise barrier installation • IEC noise	• Approach ramp sheet piling, pre-bored piling and top soil removal works • Bridge Demolition / Construction • Hotel Carpark Reinstatement • Bridge E noise barrier installation • IEC noise enclosure/barrier installation	• Approach ramp sheet piling, pre-bored piling and top soil removal works • Bridge Demolition / Construction • Pier 30-32 Cap Construction • Bridge E noise barrier installation • IEC noise enclosure/barrier installation • Excavation / Construction

- enclosure/barrier installation - Excavation / Construction of retaining wall	- Excavation / Construction of retaining wall - Removal of temporary works including beams, columns and footings for TB bridge	- of retaining wall - FEHD Metal Roof Construction - Pre-bored H-piles for Approach Ramp Construction

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West under FEP-09/364/2009/B and FEP-12/364/2009/D

Table VI Principal Work Activities for Contract no. HK/2012/08

March 2017	April 2017	May 2017
- Grouting - Construction of MVB and CWB Tunnel and Slip Road 1 - Construction of drainage - Back-filling at CWB tunnel	- Grouting - Construction of MVB and CWB Tunnel and Slip Road 1 - Construction of drainage - Back-filling at CWB tunnel	- Grouting - Construction of Slip Road 1 - Construction of drainage

Contract no. HY/2010/08 – Central and WanChai Bypass – Slip road 8 section under FEP-10/364/2009B

Table VII Principal Work Activities for Contract no. HY/2010/08

March 2017	April 2017	May 2017
- Tree protection works next to existing BGO, - Drainage improvement works, - Utility diversion works, - Retaining wall works - ELS works, - Construction works for subway extension	- Tree protection works next to existing BGO, - Drainage improvement works, - Utility diversion works, - Retaining wall works - ELS works, - Construction works for subway extension	- Tree protection works next to existing BGO, - Drainage improvement works, - Utility diversion works, - Retaining wall works - ELS works, - Construction works for subway extension

Contract no. HY/2011/08 –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009B

Table VIII Principal Work Activities for Contract no. HY/2011/08

March 2017	April 2017	May 2017
• Construction of Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building • Construction of Tunnel Thermal Barrier • Installation of Electricals and Mechanicals • Installation of Tunnel Features	• Construction of Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building • Construction of Tunnel Thermal Barrier • Installation of Electricals and Mechanicals • Installation of Tunnel Features	• Construction of Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building • Construction of Tunnel Thermal Barrier • Installation of Electricals and Mechanicals • Installation of Tunnel Features

Noise Monitoring

- iii. Noise monitoring was conducted at M1a - Harbour Road Sports Center; M2b - Noon-day gun area; M3a - Tung Lo Wan Fire Station; M4b - Victoria Center; M5b - City Garden, M6 - HK Baptist Church Henrietta Secondary School, M7e and M7w – International Finance Centre eastern and western wing, and M8 – City Hall on a weekly basis.
- iv. With respect to the demolition of Ex-Harbour Road Sports Centre, the respective noise monitoring station M1a – Harbour Road Sports Centre were finely adjusted on 16 and 25 May 2017 and thereafter to the Footbridge for Harbour Road Sports for noise monitoring.
- v. Three limit level exceedance were recorded at M6 – HK Baptist Church Henrietta Secondary School on 03, 10 and 26 April 2017 in the reporting month. The exceedances were concluded as non Project related.
- vi. One limit level exceedance was recorded at M5b – City Garden on 18 April 2017. The exceedance was concluded as Project related.
- vii. Two limit level exceedances were recorded at M1a – Footbridge for Ex-Harbor Road Sports Centre on 16 and 25 May 2017 in the reporting month. The exceedances were concluded as non Project related.

Real time Noise Monitoring

- viii. 24-hour real time noise monitoring was conducted at RTN1 - FEHD Hong Kong Transport Section Whitefield Depot for the pilling works in FEHD Whitfield Depot and RTN2 – Tunnel (North Point Section) and Island Eastern Corridor Link during the period from 28 September 2012 til 10am on 5 October 2012 in the reporting period.
- ix. Real time noise monitoring station at Oil Street Community Liaison Centre (RTN2- Oil Street Community Centre) was relocated from Oil Street Community Liaison Centre to Hong Kong Electric (RTN2a- Electric Centre) on 5 Oct which is a representative of the noise sensitive receiver City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted in Electric Centre from 4 December 2009 to 17 December 2009.
- x. As confirmed by CWB RSS, the IECL parapet removal operations will commence in March 2013. Liaison was conducted with HK Baptist Church Henrietta Secondary School and Po Leung Kuk Yu Lee Mo Fan Memorial School regarding the set up of RTN3 real time noise monitoring station. Po Leung Kuk Yu Lee Mo Fan Memorial School grant permission for set up on 4 Sep 2012 and station set up was performed on 14 Sep 2012.
- xi. Real Time Noise Monitoring at RTN3- Po Leung Kuk Yu Lee Mo Fan Memorial School was commenced since 06 Oct 2012.
- xii. Causeway Bay Community Centre has granted permission for set up of real time noise monitoring station on 21 Dec 2012 and station set up was performed on 27 Dec 2012. The Baseline noise level of RTN4- Causeway Bay Community Centre will adopt the results from the baseline noise monitoring report for EP/364/2009 in 22 April 2010 in which approved by EPD.
- xiii. According to clause 3.1 stated in EP-364/2009B, “the real-time monitoring system shall be in place no later than two weeks before the commencement date of demolition works of the existing Island Eastern Corridor”. IEC demolition associated construction works was commenced on 3 Feb 2013 and Real time noise monitoring at RTN4-Causeway Bay Community Centre was commenced on 13 Jan 2013.

- xiv. Real-time noise monitoring station RTN1-FEHD Whitfield Depot was finely adjusted from 2/F to roof-top at FEHD Whitfield Depot on 24 June 2013 with respect to the commencement of advance works for IEC parapet demolition.
- xv. With respect to the non-CWB Project building construction at Oil Street, the real-time noise monitoring station RTN2a- Hong Kong Electric Centre was finely adjusted from Northeast Side to Northwestern side at Roof Top location.
- xvi. No limit level exceedance was recorded in March, April and May reporting month at RTN1-FEHD Hong Kong Transport Section Whitfield Depot during this reporting period.
- xvii. No project related exceedance was recorded in March and May reporting month and no limit level exceedance was recorded in April reporting month at RTN2a-Hong Kong Electric Centre during this reporting period.
- xviii. No limit level exceedance was recorded in March and April reporting month and no project related exceedance was recorded in May reporting month at RTN3-Yu Lee Mo Fan Memorial School during this reporting period.
- xix. No limit level related exceedance was recorded in March and May reporting month and no project level exceedance was recorded in April reporting month at RTN4- Causeway Bay Community Centre in the reporting period.

Air Quality Monitoring

- xx. Due to extension of site boundary by contractor of HY/2009/19, location of air quality monitoring station CMA1b – Oil Street Community Liaison Centre has been finely adjusted on 21 April 2012.
- xxi. With respect to the proposed demolition of eastern podium of Oil Street Site Office, the respective air quality monitoring station CMA1b – Oil Street Site Office was finely adjusted from East podium of the Oil Street Site Office to the West podium of the Oil Street Site Office on 21 December 2016.
- xxii. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted at CMA1b - Oil Street Community Liaison Centre; CMA2a - Causeway Bay Community Center; CMA3a - CWB PRE Site Office Area; CMA4a – Society for the Prevention of Cruelty to Animals; CMA5b – Pedestrian Plaza; MA1e and MA1w – International Finance Centre eastern and western wing on every six days basis.
- xxiii. One 1hr TSP limit level exceedance was recorded at CMA1b- Oil Street Site Office on 27 March 2017 in the reporting month. The exceedance was concluded to be non-Project related.
- xxiv. One 1hr TSP limit level exceedances were recorded at CMA4a – Society for the Prevention of Cruelty to Animals on 03 March 2017 in the reporting month. The exceedance was concluded to be non-Project related.
- xxv. One 24hr TSP limit level exceedance was recorded at CMA5b – Pedestrian Plaza on 02 March 2017 in the reporting month. The exceedance was concluded to be non-Project related.
- xxvi. Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedance were recorded at CMA5b –Pedestrian Plaza on 03 March 2017 in the reporting month. The exceedances were concluded to be non-Project related.

Complaints, Notifications of Summons and Successful Prosecutions

- xxvii. Five environmental complaints were received in the reporting quarter.
- xxviii. First ICC complaint referred by RSS was received by ET on 27 February 2017 (CASE#2-3521097579). The complainant reported that noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.

ET confirmed with the Resident Site Staff that no construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017.

No construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017.

Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

- xxix. Second ICC complaint referred by RSS was received by ET on 06 March 2017 (CASE#2-3576157538). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.

The ICC complaint was subsequently referred to the EPD. EPD subsequently refer the same complaint case to the ET on 14 March 2017 (EPD Ref: H05/RS/0006240-17). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.

ET confirmed with the Resident Site Staff that no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 no. of loader were in operation below ground level.

According to the information confirmed by RSS, no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to

1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 loader were in operation below ground level. Relevant Construction Noise Permit GW-RS1305-16 was in place.

Nevertheless, in view of the public concern, the Contractor of HK/2009/02 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HK/2009/02 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

- xxx. Third ICC complaint referred by RSS was received by ET on 13 March 2017 (CASE#2-3603182890). The complainant reported that noise was emanated from the construction Site at Victoria Park from 2300hrs to 2400hrs on 10 March 2017 and caused nuisance to nearby residents.

ET confirmed with the Resident Site Staff that no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.

Based on the information provided by the RSS, no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.

Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

- xxxi. Forth EPD complaint was referred to the ET on 18 May 2017 (CASE Ref: H05/RS/00014415-17(14448-17). The complainant reported that construction work was found on 10 May 2017 (~03:52) that caused noise nuisance. According to the photos provided by the complainant lorry mounted concrete pump were used. According to the information provided by the IEC on 11 May 2017 and 15 May 2017, it was alleged that the concreting work under Contract No. HK/2009/02 was carried out for the Central-Wan Chai Bypass Top Slab Bay 6 during night time on 09 May 2017 and early morning on 10 May 2017 (between 11:00pm on 09 May 2017 and about 04:00 a.m. on 10 May 2017) with 3 pump trucks, 10 vibrating pokers, 9 concrete trucks and 2 generators in operation. The concreting works under Contract No. CEDD HK/2009/02 was also carried out for the Central – Wan Chai Bypass Bay 10A OHVS Slab after 23:00 on 12 May 2017 (after 23:00) with 1 Pump truck, 2 vibrating pokers, 1 concrete trucks and 3 generators in operation.

ET confirmed with the Resident Site Staff that 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in

operation at around 0320hrs on 10 May 2017. 2 nos. of vibratory pokers, 1 no. of concrete truck, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017.

According to the RSS site information, 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generator were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 11 May 2017, ad-hoc inspection was conducted by the Environmental Team on 13 May 2017 around 00:40 hrs. No construction operation and no PME deployment was observed at the time of inspection.

According to the RSS site information, 2 nos. of vibratory pokers, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017 and could not comply with the item 3a - PME requirement under Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 15 May 2017, ad-hoc inspection was conducted by the Environmental Team on 19 May 2017 around 22:20hrs. 2 nos. of concrete truck, 1 no. of concrete pump truck were observed in operation at the time of inspection and relevant CNP GW-RS0334-17 was in place.

Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Contractor of HK/2009/02 is also recommended to provide briefing and training session to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/2009/02 during restricted hours and report relevant findings, if any, accordingly.

- xxxii. Fifth EPD complaint was referred to the ET on 25 May 2017 (CASE Ref: N/A). The complainant reported that concreting works under Contract No. CEDD HK/2009/02 was carried out with crawler cranes, 10-12 vibratory pokers, and 7 concrete lorry mixers in the morning on 21 May 2017 without a valid CNP. Also, at 15:30 on 21 May 2017, 9 vibratory pokers and 7 concrete lorry mixers were observed in operation. These works were suspected to contravene the Noise Control Ordinance (NCO).

ET confirmed with the Resident Site Staff that 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 3 nos. of crawler cranes were

operated at Tunnel Portion 5 from 0800hrs to 0915hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017. 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs on 21 May 2017. 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 7 nos. of concreting trucks were operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017.

According to the RSS site information, the following PME were operated on 21 May 2017, i) 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs; ii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs; iii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017; iv) 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs; v) 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs ; 7 nos. of concreting trucks were operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS334-17.

EPD notification on the cancellation of the Construction Noise Permits GW-RS0334-17 and Construction Noise Permit GW-RS1297-16 was received by the Environmental Team on 26 May 2017. Ad hoc inspection was conducted by the Environmental Team on 26 May 2017 around 2230hrs and on 28 May 2017 around 1520hrs and no construction works and no operation of PME was observed at the concerned site Portion 5 at the time of inspections. Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Contractor of HK/2009/02 is also recommended to provide briefing and training session to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/2009/02 during restricted hours and report relevant findings, if any, accordingly.

- xxxiii. According to the information provided to the Environmental Team on 31 March 2017, four Summons to defendants were issued to the Contractor(s) of Contract HY/2009/19.
- xxxiv. Two Summons to Defendant (Case No. ESS40680/2016 and Case No. ESS40679/2016) were issued to the Contractor(s) under Contract HY/2009/19 on 25 October 2016 regarding the case against Section 6(1)(b) and 6(5), Noise Control Ordinance Cap 400.
- xxxv. Two Summons to Defendant (Case No. ESS38444/2016 and Case No. ESS38443/2016) were issued to the Contractor(s) under Contract HY/2009/19 on 06 October 2016 regarding the



- case against (Regulations 4(1) and 4(2) of the Air Pollution Control (Construction Dust) Regulation made under section 43 of the Air Pollution Control Ordinance, Cap311.
- xxxvi. The offence under the two Summons to Defendant (Case No. ESS38444/2016 and Case No. ESS38443/2016) issued to the Contractor(s) under Contract HY/2009/19 on 06 October 2016 regarding the case against (Regulations 4(1) and 4(2) of the Air Pollution Control (Construction Dust) Regulation made under section 43 of the Air Pollution Control Ordinance, Cap311 were convicted on 03 April 2017.
- xxxvii. Two Summons to Defendant (Case No. ESS40680/2016 and Case No. ESS40679/2016) were issued to the Contractor(s) under Contract HY/2009/19 on 25 October 2016 regarding the case against Section 6(1)(b) and 6(5), Noise Control Ordinance Cap 400 were convicted on 04 May 2017.

1. INTRODUCTION

1.1 Scope of the Report

1.1.1. Lam Geotechnics Limited (LGL) has been appointed to work as the Environmental Team (ET) under Environmental Permit no. EP-364/2009/E and Further Environmental permit nos. FEP-01/364/2009, FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A, FEP-07/364/2009/D, FEP-09/364/2009/B, FEP-10/364/2009/B, FEP-11/364/2009/B and FEP-12/364/2009/D to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) and in the EM&A Manual of the approved EIA Report for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001).

1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 10.3 of EM&A Manual and “*Environmental Monitoring and Audit Requirements*” under Particular Specification Section 27.

1.1.3. This report documents the finding of EM&A works during the period from [27 February 2017 to 26 May 2017](#).

1.2 Structure of the Report

Section 1	<i>Introduction</i> – details the scope and structure of the report.
Section 2	<i>Project Background</i> – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
Section 3	<i>Monitoring Requirements</i> – summarizes all monitoring parameters, monitoring locations, monitoring frequency, duration and action plan.
Section 4	<i>Monitoring Results</i> – summarizes the monitoring results obtained in the reporting period.
Section 5	<i>Compliance Audit</i> – summarizes the auditing of monitoring results, all exceedances environmental parameters.
Section 6	<i>Complaints, Notification of summons and Prosecution</i> – summarizes the cumulative statistics on complaints, notification of summons and prosecution
Section 7	<i>Cumulative Construction Impact due to the Concurrent Projects</i> – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.
Section 8	<i>Conclusion</i>

2. PROJECT BACKGROUND

2.1 Background

2.1.1. “Wan Chai Development phase II and Central-Wan Chai Bypass” and “Central-Wan Chai Bypass and Island Eastern Corridor Link” (hereafter called “the Project”) are Designed Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001) and Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) have been approved on 31 August 2001 and 11 December 2008 respectively.

2.1.2. The key purpose of Wan Chai Development Phase II (WDII) is to provide land at Wan Chai North and North Point for construction of the Central-Wan Chai Bypass and Island Eastern Corridor Link (CWB). Land formed under the project will be developed as a world-class waterfront promenade joining that at the new Central waterfront for public enjoyment.

2.1.3. There is a compelling and present need for the CWB to provide relief to the very congested east-west Connaught Road Central/Harcourt Road / Gloucester Road Corridor (the Corridor) which is currently operating beyond its capacity. The CWB will provide relief to the existing congestion along the Corridor and cater for the anticipated growth of traffic on Hong Kong Island. Without the CWB and its access roads, there will not be sufficient capacity to serve the heavy traffic demands at both strategic and local levels.

2.2 Scope of the Project and Site Description

2.2.1. Design and Construction of Central – Wan Chai Bypass and Island Eastern Corridor Link under the Project involves the construction and operation of a trunk road and its road tunnel more than 800m in length between portals that is shown at [Figure 2.1](#).

2.2.2. The study area encompasses existing developments from Central to North Point. The scope of the Central-Wanchai Bypass (CWB) and Island Eastern Corridor Link (IECL) includes:

- A dual three-lane trunk road, approximately 4.5 km in length, and tunnel approximately 3.7 km in length defined from the connection with the existing Rumsey Street Flyover in Central, through to a connection with the existing Island Eastern Corridor to the east of the Causeway Bay Typhoon Shelter (CBTS);
- The Central Interchange near the Rumsey Street Flyover to provide road connections to the Central area;
- Tunnel control buildings and ventilation buildings;
- Slip roads to connect the CWB to the local road system in the Wan Chai North and Causeway Bay area;
- Associated road lighting, road signing, traffic control and surveillance system; and
- Other associated works.

2.2.3. The project also contains various Schedule 2 DPs that, under the EIAO, require Environmental Permits (EPs) to be granted by the DEP before they may be either constructed or operated. **Table 2.1** summarises the five individual DPs under this Project. **Figure 2.1** shows the locations of these Schedule 2 DPs.

Table 2.1 Schedule 2 Designated Projects under this Project

Item	Designated Project	EIAO Reference	Reason for inclusion
DP1	Central-Wanchai Bypass (CWB) including its road tunnel and slip roads	Schedule 2, Part I, A.1 and A.7	Trunk road and road tunnel more than 800 m in length
DP2	Road P2 and other roads which are classified as primary/district distributor roads	Schedule 2, Part I, A.1	Primary / district distributor roads
DP3	Reclamation works including associated dredging works	Schedule 2, Part I, C.1 and C.12	Reclamation more than 5 ha in size and a dredging operation less than 100 m from a seawater intake point
DP5	Wan Chai East Sewage Outfall	Schedule 2, Part I, F.5 and F.6	Submarine sewage pipelines with a total diameter more than 1,200 mm and include a submarine sewage outfall
DP6	Dredging for the Cross-harbour Water Mains from Wan Chai to Tsim Sha Tsui	Schedule 2, Part I, C.12	A dredging operation less than 100 m from a seawater intake point

2.3 Division of the Project Responsibility

2.3.1. Due to the multi-contract nature of the Project, there are a number of contracts sub-dividing the whole works area into different work areas to be commenced. Contractors of individual contracts will be required by the EP holder to apply Further Environmental Permits such that the impact monitoring stations are sub-divided accordingly to facilitate the implementation of EM&A programme and to streamline the EM&A reporting for individual FEP holders correspondingly.

2.3.2. In the reporting period, all the contracts were commenced and contract no. 04/HY/2006 had been completed. The details of individual contracts are summarized in **Table 2.2**.

Table 2.2 Details of Individual Contracts under the Project

Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
HY/2009/17	Central – Wan Chai Bypass (CWB) at FEHD Whitfield Depot – Advanced piling works.	DP1	5 October 2010 (Completed)
HY/2009/18	Central – Wan Chai Bypass (CWB) – Central Interchange	DP1	21 April 2011
04/HY/2006	Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street	DP1	September 2010 (Completed)
HK/2009/01	Wan Chai Development Phase II – Central – Wan Chai Bypass at Hong Kong Convention and Exhibition	DP1, DP2	25 August 2011

Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
	Centre – Tunnel Works		
HK/2009/02	Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East(CWB Tunnel)	DP1	26 April 2011
HY/2009/15	Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)	DP1	13 July 2011
HY/2009/19	Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link	DP1	24 March 2011
HK/2010/06	Wan Chai Development Phase II- Central-Wan Chai Bypass over MTR Tsuen Wan Line	DP3	22 March 2011 (Completed)
HK/2012/08	Wan Chai Development Phase II- Central-Wan Chai Bypass at Wan Chai West	DP1,DP2, DP3	10 March 2014
HY/2010/08	Central- Wanchai Bypass Tunnel – Tunnel (Slip Road 8)	DP1, DP2, DP3	21 March 2013
HY/2011/08	Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning	DP1	8 October 2014

- 2.3.3. The construction works of Contract no. 04/HY/2006 – Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street under FEP-04/364/2009/A was completed, and the FEP was surrendered by the Contractor on 11 February 2011.
- 2.3.4. Construction of bored pile E3B under HY/2009/17 was confirmed completed and the respective work area under FEP-03/364/2009 was handover and inspected under HY/2009/19 from 19 Dec 2012 onwards. Subsequently, the FEP-03/364/2009 was surrendered by the Contractor on 28 March 2013.
- 2.3.5. Construction works under HK/2010/06 was confirmed completed and the respective work area under FEP-08/364/2009/A was handover and inspected under HK/2012/08 from 22 Sep 2014 onwards. Subsequently, the FEP-08/364/2009/A was surrendered by the Contractor on 3 October 2014.

2.4 Project Organization and Contact Personnel

- 2.4.1. Civil Engineering and Development Department and Highways Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.4.2. The proposed project organization and lines of communication with respect to environmental protection works are shown in [Figure 2.2](#). Key personnel and contact particulars are summarized in **Table 2.3**.

Table 2.3 Contact Details of Key Personnel

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3916 1818	3529 2829
Chun Wo – Leader Joint Venture	Contractor under Contract no. HK/2009/01	Site Agent	Mr. Andy Yu	9648 4896	2634 1626
		Construction Manager	Mr. Terry Wong	9757 9846	
		Construction Manager	Mr. Terry Tsang	6683 9394	
Chun Wo – CRGL Joint Venture	Contractor under Contract no. HK/2009/02	Site Agent	Mr. Paul Yu	3658-3002	2827 9996
		Environmental Officer	Mr. C.P. Ho	9191 8856	
Chun Wo - CRGL - MBEC Joint Venture	Contractor under Contract no. HY/2009/19	Project Manager	Mr. Rayland Lee	3758 8879	2570 8013
		Deputy Project Manager	Mr. William Luk	9456 9819	
		Site Agent	Mr. David Lau	3758 8879	
		Deputy Site Agent	Mr. Eric Fong	6191 9337	
		Environmental Manager / Environmental Officer	Mr. M.H. Isa	3757 8218	
		Assistant Environmental Officer	Mr. James Chan	3757 8217	
Leighton Contractors (Asia) Limited	Contractor under Contract no. HY/2009/18	Site Agent	Mr. Jimmy Chu	2214 7700	2140 6799
		Environmental Officer	Mr. Chris Chan	2823 1161	
		Assistant Environmental Engineer	Mr. Christy So	3937 1065	

Party	Role	Post	Name	Contact No.	Contact Fax
China State Construction Engineering (HK) Ltd.	Contractor under Contract no. HY/2009/15	Contractor's Representative	Mr. Rex Chan	3557 6371	2566 2192
		Environmental Officer	Mr. Andy Mak	3557 6215	
China State-Leader JV	Contractor under Contract no. HK/2012/08	Project Director	Mr. C.N. Lai	9137 1811	2877 1522
		Project Manager	Mr. Eddie Chung	9193 8871	
		Site Agent	Mr. Keith Tse	9095 7922	
		Environmental Officer	Mr. James MA	9130 9549	
		Environmental Supervisor	Mr. Y.L. Ho	6050 4919	
China State	Contractor under Contract no. HY/2010/08	Project Director	Cheung Kit Cheung	3557 6399	3465 2899
		Project Manager	Chan Ying Lun	9812 0592	
		Deputy Project Manager	Chris Leung	3467 4299	
		Site Agent	Mr. Francis Suen	3467 4277	
		Environmental Officer	Mr. Gabriel Wong	3557 6464	
		Assistant Environmental Officer	Mr. Desmond Ho	3557 6470	
Leighton Joint Venture	Contractor under Contract no. HY/2011/08	Project Manager	Paul Evans	2823 1111	21406799
		Site Agent	Colman Wong	9730 0806	
		Environmental Officer	Malcom Leung	3973 0850	
		Environmental Supervisor	Christy So	3973 1065	
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331
RAMBOLL ENVIRON Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899

2.5 Principal Work and Activities

2.5.1. Major construction activities for Contract no. HY/2009/18 have been commenced on 21 April 2011. During this reporting period, the principal work activities for Contract no. HY/2009/18 are summarized in **Table 2.4**:

Table 2.4 Principal Work Activities for Contract no. HY/2009/18

March 2017	April 2017	May 2017
• Drainage works • Road works • Landscaping works • Maintenance works	• Drainage works • Road works • Landscaping works • Maintenance works	• Drainage works • Road works • Landscaping works • Maintenance works

2.5.2. Major construction activities for Contract no. HK/2009/01 have been commenced on 25 August 2011. During this reporting period, the principal work activities are summarized in **Table 2.5**:

Table 2.5 Principal Work Activities for Contract no. HK/2009/01

March 2017	April 2017	May 2017
• Reinstatement of amenity area • Road and Drain works	• Reinstatement of amenity area • Road and Drain works	• Reinstatement of amenity area • Road and Drain works

2.5.3. Major construction activities for Contract no. HK/2009/02 have been commenced on 26 April 2011. During this reporting period, the principal work activities are summarized in **Table 2.6**:

Table 2.6 Principal Work Activities for Contract no. HK/2009/02

March 2017	April 2017	May 2017
• Defective works for Star Ferry Pier • Rectification works for cross road ducts • Rectification works for cracks/joints with water leakage inside OHVD cells • Removal works for ELS S1 • Demolition works for Hung Hing Road Flyover abutment • Backfilling works • Temporary wall for construction of Hung Hing Road Flyover • Concreting mass concrete	• Rectification works for the defects recorded in the inspection for the end of maintenance period of Observation Deck and Staircase ST-01 • Rectification works for cross road ducts • rectification works for cracks/joints with water leakage inside OHVD cells • Backfilling works • Construction of temporary wall for inside tunnel • Blinding layer for Hung Hing Road Flyover • Cleaning of cross road	• Rectification works for the defects recorded in the inspection for the end of maintenance period of Observation Deck and Staircase ST-01 • completion of rectification works for cracks/joints with water leakage inside OHVD cells • backfilling works • construction of temporary wall for inside tunnel • blinding layer for Hung Hing Road Flyover • demolition of diaphragm wall for reinstatement of Hung Hing Road approach

- underneath Hung Hing Road Flyover • Delivery of precast concrete seawall block • Cleaning of cross road duct & carrier drain • Rectification works against water leakage and remedial works against concrete defects of the tunnel structure • Waterproofing laying work • Concreting for base slab • Removal of ELS layer S2 & S3 • Tunnel wall structure • Concreting for roadside barrier • Erection of scaffolding for construction of OHVD • Excavation works for trial pit for the 132kV HK Electric Cables	- duct & carrier drain • Rectification works against water leakage and remedial works against concrete defects of the tunnel structure • Outstanding works inside tunnel • Concreting for base slab • Removal of ELS layer S2 & S3 • Tunnel wall structure • Concreting for roadside barrier • Erection of scaffolding for construction of OHVD • Concreting for OHVD slab • Erection of scaffolding for construction of top slab	- ramp • cleaning of cross road duct • Rectification works against water leakage and remedial works against concrete defects of the tunnel structure • outstanding works inside tunnel • Tunnel wall structure • Concreting for roadside barrier • Erection of scaffolding for construction of OHVD • Concreting for OHVD slab • Erection of scaffolding for construction of top slab • Tunnel top slab • Rectification work for road defects at Wan Shing Street

2.5.4. Major construction activities for Contract no. HY/2009/15 have been commenced on 13 July 2011. During this reporting period, the principal work activities are summarized in **Table 2.7**:

Table 2.7 Principal Work Activities for Contract no. HY/2009/15

March 2017	April 2017	May 2017
• Remedial works inside tunnel structure at Mined Tunnel, TS4, TPCWAE and TPCWAW • Reinstatement of drainage pipes and manhole at TPCWAE	• Remedial works inside tunnel structure at Mined Tunnel, TS4, TPCWAE and TPCWAW • Reinstatement work at the PRE Office car park area	• Remedial works inside tunnel structure at Mined Tunnel, TS4, TPCWAE and TPCWAW • Reinstatement work at the PRE Office car park area

2.5.5. Major construction activities for Contract no. HY/2009/19 have been commenced on March 2011. During this reporting period, the principal work activities are summarized in **Table 2.8**:

Table 2.8 Principal Work Activities for Contract no. HY/2009/19

March 2017	April 2017	May 2017
• Approach ramp sheet piling, pre-bored piling and top soil removal works	• Approach ramp sheet piling, pre-bored piling and top soil removal works	• Approach ramp sheet piling, pre-bored piling and top soil removal works • Bridge Demolition /

• Hing Fat Street modification works • Bridge Demolition / Construction • Hotel Carpark Reinstatement • Bridge E noise barrier installation • IEC noise enclosure/barrier installation • Excavation / Construction of retaining wall	• Bridge Demolition / Construction • Hotel Carpark Reinstatement • Bridge E noise barrier installation • IEC noise enclosure/barrier installation • Excavation / Construction of retaining wall • Removal of temporary works including beams, columns and footings for TB bridge	• Construction Pier 30-32 Cap Construction • Bridge E noise barrier installation • IEC noise enclosure/barrier installation • Excavation / Construction of retaining wall • FEHD Metal Roof Construction • Pre-bored H-piles for Approach Ramp Construction

2.5.6. Major construction activities for Contract no. HK/2012/08 have been commenced on March 2013. During the reporting period, the principal work activities are summarized in **Table 2.9**

Table 2.9 Principal Work Activities for Contract no. HK/2012/08

March 2017	April 2017	May 2017
• Grouting • Construction of MVB and CWB Tunnel and Slip Road 1 • Construction of drainage • Back-filling at CWB tunnel	• Grouting • Construction of MVB and CWB Tunnel and Slip Road 1 • Construction of drainage • Back-filling at CWB tunnel	• Grouting • Construction of Slip Road 1 • Construction of drainage

2.5.7. Major construction activities for Contract no. HY/2010/08 have been commenced on March 2013. During the reporting period, the principal work activities are summarized in **Table 2.10**

Table 2.10 Principal Work Activities for Contract no. HY/2010/08

March 2017	April 2017	May 2017
• Tree protection works next to existing BGO, • Drainage improvement works,	• Tree protection works next to existing BGO, • Drainage improvement works,	• Tree protection works next to existing BGO, • Drainage improvement works,

• Utility diversion works, • Retaining wall works • ELS works, • Construction works for subway extension	• Utility diversion works, • Retaining wall works • ELS works, • Construction works for subway extension	• Utility diversion works, • Retaining wall works • ELS works, • Construction works for subway extension

- 2.5.8. Contract no. HY/2011/08 –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009B. During the reporting period, the principal work activities are summarized in **Table 2.11**

Table 2.11 *Principal Work Activities for Contract no. HY/2011/08*

March 2017	April 2017	May 2017
• Construction of Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building • Construction of Tunnel Thermal Barrier • Installation of Electricals and Mechanicals • Installation of Tunnel Features	• Construction of Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building • Construction of Tunnel Thermal Barrier • Installation of Electricals and Mechanicals • Installation of Tunnel Features	• Construction of Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building • Construction of Tunnel Thermal Barrier • Installation of Electricals and Mechanicals • Installation of Tunnel Features

- 2.5.9. Implementation status of the recommended mitigation measures during this reporting period is presented in **Appendix 2.1**.

3. MONITORING REQUIREMENTS

3.1. Noise Monitoring

NOISE MONITORING STATIONS

- 3.1.1. The noise monitoring stations for the Project are listed and shown in **Table 3.1** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.1 Noise Monitoring Station

Station	Description
M1a	Footbridge at Ex-Harbour Road Sports Centre
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School
*M7e	International Finance Centre (Eastern End of Podium)
M7w	International Finance Centre (Western End of Podium)
M8	City Hall

* Remark 1: Location ID has been updated from M7 to M8 for City Hall

* Remark 2: M7e has become a reference station starting from 7 Aug 2012

Remarks***: The location ID of monitoring station M1a was updated as "Footbridge for Ex-Harbour Road Sports Centre" in May 2017.

REAL TIME NOISE MONITORING STATIONS

- 3.1.2. The noise monitoring stations for the Project are listed and shown in **Table 3.2** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.2 Real Time Noise Monitoring Station

District	Station	Description
Tin Hau	RTN1	FEHD Hong Kong Transport Section Whitefield Depot
North Point	RTN2a	Electric Centre
North Point	RTN3	Po Leung Kuk Yu Lee Mo Fan Memorial School
Tin Hau	RTN4	Causeway Bay Community Centre

* RTN2 was relocated from Oil Street Community Liaison Centre to Electric Centre on 05 Oct 2012 and re-designated as RTN2a.

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 3.1.3. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{eq} (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, L_{eq} (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.
- 3.1.4. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
- One set of measurements between 0700 and 1900 hours on normal weekdays.
- 3.1.5. Real time noise shall be carried out at the designated monitoring stations. The following is an initial guide on the regular monitoring frequency for each station on a 24 hours daily basis when noise generating activities are underway:
- One set of measurements between 0700 and 1900 hours on normal weekdays.
 - One set of measurements between 1900 and 2300 hours on normal weekdays and 0700 and 2300 hours on public holidays.
 - One set of measurements between 2300 and 0700 hours on next day on everyday.
- 3.1.6. If construction works are extended to include works during the hours of 1900 – 0700 as well as public holidays and Sundays, additional weekly impact monitoring shall be carried out during respective restricted hours periods. Applicable permits under NCO shall be obtained by the Contractor.

MONITORING EQUIPMENT

- 3.1.7. As referred to in the Technical Memorandum TM issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.
- 3.1.8. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.
- 3.1.9. The sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency before deployment to the site and during each site

visit. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.

3.2. Air quality monitoring

AIR QUALITY MONITORING STATIONS

- 3.2.1. The air quality monitoring stations for the Project are listed and shown in **Table 3.3** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.3 Air quality monitoring Stations

Station ID	Monitoring Location	Description
CMA1b	Oil Street Site Office*	North Point
CMA2a	Causeway Bay Community Centre	Causeway Bay
CMA3a	CWB PRE Site Office	Causeway Bay
CMA4a	Society for the Prevention of Cruelty to Animals	Wan Chai
CMA5b	Pedestrian Plaza**	Wan Chai
MA1e	International Finance Centre (Eastern End of Podium)	Central
MA1w	International Finance Centre (Western End of Podium)	Central

Remarks*: The location ID of monitoring station CMA1b was updated as "Oil Street Site Office" in April 2013. With respect to the removal of Oil Street Site Office, the respective air quality monitoring station CMA1b was finely adjusted on 11 September 2015.

Remarks**: With respect to the area handover, the air quality monitoring station CMA5a at Children Playgrounds opposite to the Pedestrian Plaza was relocated to the Pedestrian Plaza on 3 December 2014. The station reference and location ID of the air quality monitoring station CMA5a was updated as CMA5b and Pedestrian Plaza respectively.

Remarks***: The location ID of monitoring station M1a was updated as "Footbridge for Ex-Harbour Road Sports Centre" in May 2017.

AIR QUALITY MONITORING PARAMETERS, FREQUENCY AND DURATION

- 3.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 3.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.

- 3.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 3.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
- 0.6 – 1.7 m³ per minute adjustable flow range;
 - Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
 - Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
 - Capable of providing a minimum exposed area of 406 cm²;
 - Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
 - Equipped with a shelter to protect the filter and sampler;
 - Incorporated with an electronic mass flow rate controller or other equivalent devices;
 - Equipped with a flow recorder for continuous monitoring;
 - Provided with a peaked roof inlet;
 - Incorporated with a manometer;
 - Able to hold and seal the filter paper to the sampler housing at horizontal position;
 - Easily changeable filter; and
 - Capable of operating continuously for a 24-hour period.
- 3.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.
- 3.2.7. Laboratory Measurement / Analysis
- 3.2.8. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.
- 3.2.9. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 3.2.10. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with



readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.

3.2.11. All the collected samples shall be kept in a good condition for 6 months before disposal.

4. MONITORING RESULTS

- 4.0.1. Per EPD's letter dated 3 Aug 2012 (received by ET on 6 Aug 2012 through HyD), noise monitoring at M8 – City Hall commenced on 7 Aug 2012, and the monitoring station M7e – International Finance Centre (Eastern Podium) has become a reference station starting from 7 Aug 2012.
- 4.0.2. Due to safety concerns, the monitoring location for M4b – Victoria Centre has been finely adjusted from 7 June 2012.
- 4.0.3. Monitoring for report of review baseline noise level was performed from 11 April 2011 to 8 June 2011. Then the report was submitted on the 20 June 2011, verified by IEC on 18 July 2011 and was approved by ER by January 2012. The new baseline is used for the noise calculation starting from the January 2012 reporting month.
- 4.0.4. The environmental monitoring will be implemented based on the division of works areas of each designed project managed under different contracts with separate FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in **Figure 2.1** and **Figure 3.1**. The monitoring results are presented in according to the Individual Contract(s).
- 4.0.5. In the reporting period, the concurrent contracts are as follows:
- Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A
 - Contract no. HY/2009/18 – Central –Wanchai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A
 - Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009
 - Contract no. HK/2009/01 –Wanchai Development Phase II – Central –Wanchai Bypass at Hong Kong Convention and Exhibition Centre under FEP-02/364/2009
 - Contract no. HK/2009/02 Wanchai Development Phase II – Central- Wanchai Bypass at Wanchai East under FEP-01/364/2009
 - Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West under FEP-09/364/200/B
 - Contract no. HY/2010/08 – Central and WanChai Bypass – Slip road 8 Section under FEP-10/364/2009/B
 - Contract no. HY/2011/08 –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/B

4.1. Noise Monitoring Results

Contract no. HY/2009/18 – Central – Wanchai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- 4.1.1. Noise monitoring for the Central Interchange works under contract no. HY/2009/18 was commenced on 22 April 2011. The proposed division of noise monitoring stations for Contract no. HY/2009/18 are summarized in **Table 4.1** below.

Table 4.1 Noise Monitoring Station for Contract no. HY/2009/18

Station	Description
*M7e	International Finance Centre (Eastern End of Podium)
M7w	International Finance Centre (Western End of Podium)
M8	City Hall

* Remark: M7e has become a reference station starting from 7 Aug 2012

- 4.1.2. No exceedance was recorded in this reporting quarter.
- 4.1.3. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in [Appendix 4.1](#).

Contract no. HK/2009/01 - Wanchai Development Phase II - Central - Wanchai Bypass at Hong Kong Convention and Exhibition Centre - Tunnel Works under FEP-02/364/2009 and Contract no. HK/2009/02 - Wanchai Development Phase II - Central - Wanchai Bypass at Wanchai East (CWB Tunnel) under FEP-01/364/2009

- 4.1.4. The commencement of construction works for Contract no. HK/2009/01 under FEP-02/364/2009 is on 25 August 2011 and HK/2009/02 under FEP-01/364/2009 is on 26 April 2011. The proposed division of air quality monitoring stations are summarized in **Table 4.2** below.

Table 4.2 Noise Monitoring Stations for Contract nos. HK/2009/01 and HK/2009/02

Station	Description
M1a	Footbridge at Ex-Harbour Road Sports Centre

[Reporting Month of March 2017](#)

- 4.1.5. [No action or limit level exceedance was recorded in this reporting month.](#)

[Reporting Month of April 2017](#)

- 4.1.6. [No action or limit level exceedance was recorded in this reporting month.](#)

Reporting Month of May 2017

- 4.1.7. Two limit level exceedances were recorded at M1a – Footbridge for Ex-Harbour Road Sports Centre on 16 and 25 May 2017 in the reporting month.
- 4.1.8. No Construction works was conducted under Contract HK/2009/01 around the monitoring station on 16 and 25 May 2017, non WDII-CWB Projects breaking and drilling works was observed on 16 May 2017 and non WDII-CWB Project bored pilling works was conducted on 25 May 2017 during monitoring period and observed as the major noise contribution. Hence, the exceedances were considered as non-Project related.
- 4.1.9. Despite rebar fixing, and formwork fixing works was conducted on 16 May 2017 and rebar fixing was conducted on 25 May 2017 under Contract HK/2009/02, non WDII-CWB Projects breaking and drilling works was observed on 16 May 2017 and non WDII-CWB Project bored pilling works was conducted on 25 May 2017 during monitoring period and observed as the major noise contribution. Hence, the exceedances were considered as non-Project related.
- 4.1.10. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 4.1**.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- 4.1.11. The commencement of construction works for Contract no. HY/2009/15 under FEP-06/364/2009/A was on 13 July 2011. Noise monitoring was commenced on 13 July 2011. The proposed division of noise monitoring stations are summarized in **Table 4.3** below.

Table 4.3 Noise Monitoring Station for Contract nos. HY/2009/15

Station	Description
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station

- 4.1.12. No action or limit level exceedance was recorded in this reporting quarter.
- 4.1.13. Details of noise monitoring results and graphical presentation can be referred in **Appendix 4.1**.

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

- 4.1.14. Noise monitoring for the tunnel works under contract no. HY/2009/19 was commenced on 24 April 2011. The proposed division of noise monitoring stations are summarized in **Table 4.4** below.

Table 4.4 Noise Monitoring Stations for Contract no. HY/2009/19

Station	Description
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School

Reporting Month of March 2017

- 4.1.15. No action and limit exceedance was recorded at M6- HK Baptist Church Henrietta Secondary School in this reporting month.

Reporting Month of April 2017

- 4.1.1 Three limit level exceedances were recorded at M6 – Hk Baptist Church Henrietta Secondary School on 03, 10 and 26 April 2017 in the reporting month.
- 4.1.2 Traffic noise was observed during monitoring on 03, 10 and 26 April 2017 and were considered as the major noise contribution. As such, the limit level exceedances were concluded as non-project related.
- 4.1.3 One limit level exceedance was recorded at M5b – City Garden on 18 April 2017 in the reporting month.
- 4.1.4 Starter bar fixing works and breaking works at marine pier under Contract HY/2009/19 was conducted during the measurement on 18 April 2017, it was observed that breaking operation was the major noise contribution during measurement. It is concluded that the exceedance was Project related and the contractor was requested to submit a proposal for remediation measures following the Event and Action Plan. Actions from the remediation plan including i) Closing the opening of the temporary noise barrier ii) provide physical wrapping of breaker to dampen noise emission and iii) conduct breaking works intermittently were implemented by the Contractor and no further exceedance was recorded upon implementation of the remedial actions.

Reporting Month of May 2017

- 4.1.16. No action or limit level exceedance was recorded in this reporting month.

- 4.1.17. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in [Appendix 4.1](#) and the Notification of Exceedance can be referred in [Appendix 6.2](#).

Contract no. HY/2010/08 – Central-Wanchai Bypass –Wanchai Bypass Tunnel (Slip Road 8 Section) under FEP-09/364/2009/B

- 4.1.18. The commencement of construction works for Contract no. HY/2010/08 under FEP-10/364/2009/B was on 02 September 2013. Noise monitoring was commenced on 02 September 2013. The proposed divisions of noise monitoring stations are summarized in **Table 4.5** below.

Table 4.5 Noise Monitoring Stations for Contract no. HY/2010/08

Station	Description
M3a	Tung Lo Wan Fire Station

- 4.1.19. No action or limit level exceedance was recorded in this reporting quarter.
- 4.1.20. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in [Appendix 4.1](#).

Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning

- 4.1.21. Noise monitoring for the Central Interchange works under contract no. HY/2009/18 was commenced on 22 April 2011. The proposed division of noise monitoring stations for Contract no. HY/2009/18 are summarized in **Table 4.6** below:

Table 4.6 Noise Monitoring Stations for Contract no. HY/2011/08

Station	Description
M4b	Victoria Centre
*M7e	International Finance Centre (Eastern End of Podium)
M7w	International Finance Centre (Western End of Podium)
M8	City Hall

* Remark: M7e has become a reference station starting from 7 Aug 2012

- 4.1.22. No action or limit level exceedance was recorded in this reporting quarter.
- 4.1.23. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in [Appendix 4.1](#)

4.2. Real Time Noise Monitoring Results

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

- 4.2.1. Real time noise monitoring results measured in this reporting period are reviewed and summarized. Details of real time noise monitoring results and graphical presentation can be referred to [Appendix 4.2](#)
- 4.2.2. The proposed division of noise monitoring stations are summarized in **Table 4.7** below. Real time noise monitoring for major construction works under contract no. HY/2009/19 was commenced on 24 April 2011.

Table 4.7 Real Time Noise Monitoring Stations for Contract no. HY/2009/19

Location ID	District	Description
RTN1	Tin Hau	FEHD Hong Kong Transport Section Whitefield Depot
RTN2a	North Point	Electric Centre (Replacement of RTN2)
RTN3	North Point	Pok Leung Kuk Yu Lee Mo Fun Memorial School
RTN4	Tin Hau	Causeway Bay Community Centre

** Real time noise monitoring results and graphical presentation during night time period are for information only.*

**Real-time noise monitoring results and graphical presentation for RTN3 during restricted hours are for information only as no night classes were conducted at the educational institute.*

Reporting month of [March 2017](#)

- 4.2.3. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 4.2.4. Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre on 27, 28 February and 01, 02 and 03 March 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, sheet piling, pre bored drilling and breaking works were conducted on 27, 28 February and 01, 02 and 03 March 2017 and temporary noise barrier was generally implemented and breaking works was conducted behind physical building structure while building construction works with breaking and hammering works under non-CWB private development site at Oil Street was conducted at the building level adjacent to the noise monitoring station and were considered as the major noise contribution across the monitoring period. As such, the exceedances were considered as non-Project related.
- 4.2.5. No limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School in the reporting month.
- 4.2.6. No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre in the reporting month.

Reporting month of April 2017

- 4.2.7. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 4.2.8. No limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded in the reporting month.
- 4.2.9. No limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School in the reporting month.
- 4.2.10. Limit level exceedance was recorded at RTN4- Causeway Bay Community Centre were recorded on 20 and 21 April 2017 in the reporting month. After checking with Contractor HY/2009/19, no construction works activity was conducted on 20 and 21 April 2017 during the monitoring period while non - CWB breaking was observed conducted on the monitoring dates immediately next to the monitoring station. As such, the exceedances were concluded as non-Project related.

Reporting month of May 2017

- 4.2.11. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 4.2.12. Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded on 24 May 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, despite sheet piling works was conducted during the monitoring period, adverse weather condition under Red Rainstorm Warning Signal was considered as the major noise contribution during monitoring and hence the exceedance was concluded as non-Project related.
- 4.2.13. Limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School on 10 and 24 May 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, no construction works were conducted on 10 and 24 May 2017 around the monitoring location during the concerned period and hence the exceedances were considered to be non-Project related and potentially related to the traffic on 10 May 2017 and the adverse weather under Red Rainstorm Warning Signal on 24 May 2017.
- 4.2.14. No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre was recorded in the reporting month.
- 4.2.15. Real time noise monitoring results measured in this reporting quarter are reviewed and summarized. Details of real time noise monitoring results and graphical presentation can be referred to **Appendix 4.2**

Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning

- 4.2.16. The proposed division of noise monitoring stations are summarized in **Table 4.8** below. Real time noise monitoring for major construction works under contract no. HY/2011/08 was commenced on 19 March 2015.

Table 4.8 Real Time Noise Monitoring Stations for Contract no. HY/2011/08

Location ID	District	Description
RTN1	Tin Hau	FEHD Hong Kong Transport Section Whitfield Depot
RTN2a ¹	North Point	Hong Kong Electric Centre
RTN4	Tin Hau	Causeway Bay Community Centre

* Real time noise monitoring results and graphical presentation during restrict hours and night time period are for information only and noise during CNP period shall be controlled under NCO.

Remarks ¹: With respect to the possession of site area Portion Xa and Portion Xb since 7 March 2016 as confirmed by CWB RSS, real time noise monitoring station RTN2a was associated with Contract no. HY/2011/08 from 07 March 2016 onwards

Reporting month of [March 2017](#)

- 4.2.17. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 4.2.18. Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre on 27, 28 February and 01, 02 and 03 March 2017 during daytime in the reporting month. After checking with Contractor of HY/2011/08, formworks, bar fixing and concreting works were conducted on 27, 28 February and 01, 02 and 03 March 2017 and no particular noise was considered for the works while building construction works with breaking and hammering works under non-CWB private development site at Oil Street was conducted at the building level adjacent to the noise monitoring station and were considered as the major noise contribution across the monitoring period. As such, the exceedances were considered as non-Project related.
- 4.2.19. No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.

Reporting month of [April 2017](#)

- 4.2.1. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 4.2.2. No limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded in the reporting month.
- 4.2.3. Limit level exceedance was recorded at RTN4- Causeway Bay Community Centre were recorded on 20 and 21 April 2017 in the reporting month. After checking with Contractor

HY/2011/08, no construction works activity was conducted on 20 and 21 April 2017 during the monitoring period while non - CWB breaking was observed conducted on the monitoring dates immediately next to the monitoring station. As such, the exceedances were concluded as non-Project related.

Reporting month of May 2017

- 4.2.4. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 4.2.5. Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded on 24 May 2017 during daytime in the reporting month. After checking with Contractor of HY/2011/08, no construction works was conducted during the monitoring period and adverse weather condition under Red Rainstorm Warning Signal was considered as the major noise contribution during monitoring and hence the exceedance was concluded as non-Project related.
- 4.2.6. No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre were recorded in the reporting month.
- 4.2.7. Real time noise monitoring results measured in this reporting quarter are reviewed and summarized. Details of real time noise monitoring results and graphical presentation can be referred to **Appendix 4.2**

4.3. Air quality monitoring Results

- 4.3.1 Due to extension of site boundary by contractor of HY/2009/19, location of air quality monitoring station CMA1b – Oil Street Community Liaison Centre has been finely adjusted on 21 April 2012.

Contract no. HY/2009/18 - Central - Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- 4.3.2 Air quality monitoring for the Central Interchange works under contract no. HY/2009/18 was commenced on 21 April 2011. The proposed division of air quality monitoring stations are summarized in **Table 4.9** below.

Table 4.9 Air quality monitoring Stations for Contract no. HY/2009/18

Station	Description
MA1e	International Finance Centre (Eastern End of Podium)
MA1w	International Finance Centre (Western End of Podium)

- 4.3.3 No action or limit level exceedance was recorded in the reporting period.
- 4.3.4 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in **Appendix 4.3**.

Contract no. HK/2009/01 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Hong Kong Convention and Exhibition Centre - Tunnel Works under FEP-02/364/2009

- 4.3.5 The commencement of construction works for Contract no. HK/2009/01 under FEP-02/364/2009 is on 25 August 2011. The proposed division of air quality monitoring stations are summarized in **Table 4.10** below.

Table 4.10 Air quality monitoring Station for Contract no. HK/2009/01

Station	Description
CMA5b	Pedestrian Plaza

Reporting month of March 2017

- 4.3.6 One 24hr TSP limit level exceedance was recorded at CMA5b on 02 March 2017.
- 4.3.7 No construction works was undertaken on 02 March 2017 around Pedestrian Plaza under Contract HK/2009/01, no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.

4.3.8 Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedance were recorded at CMA5b on 03 March 2017.

4.3.9 No construction works was undertaken on 03 March 2017 around Pedestrian Plaza under Contract HK/2009/01, no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.

Reporting month of April 2017

4.3.10 No exceedance was recorded in the reporting month.

Reporting month of February 2017

4.3.11 No exceedance was recorded in the reporting month.

4.3.12 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in **Appendix 4.3**.

Contract no. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

4.3.13 The commencement of construction works for HK/2009/02 under FEP-01/364/2009 is on 26 April 2011. The proposed division of air quality monitoring stations are summarized in **Table 4.11** below.

Table 4.11 Air quality monitoring Station for Contract no. HK/2009/02

Station	Description
CMA4a	Society for the Prevention of Cruelty to Animals

Reporting month of March 2017

4.3.14 One 1hr TSP limit level exceedance was recorded at CMA4a on 03 March 2017.

4.3.15 Despite backfilling works at Portion 3&4 and tunnel structure works at Portion 5 were conducted on 03 March 2017 on the monitoring date around the monitoring station under Contractor of HK/2009/02, dust suppression measure including covering of stockpile and watering for haul road and during loading and unloading of material were implemented by the Contractor and no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and the observed renovation works next to the monitoring station.

Reporting month of April 2017

4.3.16 No exceedance was recorded in the reporting month.

[Reporting month of May 2017](#)

4.3.17 No exceedance was recorded in the reporting month.

4.3.18 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in [Appendix 4.3](#).

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

4.3.19 The commencement of construction works for Contract no. HY/2009/15 under FEP-06/364/2009/A was on 13 July 2011. The proposed division of air quality monitoring stations are summarized in **Table 4.12** below.

Table 4.12 Air quality monitoring Station for Contract no. HY/2009/15

Station	Description
CMA3a	CWB site office at Wanchai Waterfront Promenade

4.3.20 No action or limit level exceedance was recorded in the reporting period.

4.3.21 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in [Appendix 4.3](#).

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

4.3.22 Air quality monitoring for the tunnel works was commenced on 26 April 2011 for Contract no. HY/2009/19 under FEP-07/364/2009/D. The proposed division of air quality monitoring stations are summarized in **Table 4.13** below.

Table 4.13 Air quality monitoring Stations for Contract no. HY/2009/19

Station	Description
CMA1b	Oil Street Site Office
CMA2a	Causeway Bay Community Centre

[Reporting month of March 2017](#)

4.3.23 One 1hr TSP limit level exceedance was recorded at CMA1b on 27 March 2017.

4.3.24 No construction works was undertaken under Contract HY/2009/19 on the monitoring date at around Oil Street Site Office while the haul road around the concerned location was observed maintained in dampened condition and no particular observation regarding air quality impact was observed during sampling. In view of the above, the limit level exceedance was considered to be non-project related and contributed by local ambient condition.

Reporting month of April 2017

- 4.3.25 No exceedance was recorded in the reporting month.

Reporting month of May 2017

- 4.3.26 No exceedance was recorded in the reporting month.
- 4.3.27 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in [Appendix 4.3](#).

Contract no. HK/2012/08- Wan Chai Development Phase II – Central-Wan Chai Bypass at Wan Chai West under FEP-09/364/2009/B and FEP-12/364/2009/D

- 4.3.28 The commencement of construction works for Contract no. HK/2012/08 under FEP-09/364/2009/C was on May 2014. Air quality monitoring was commenced on 14 July 2011. The proposed division of air quality monitoring stations are summarized in **Table 4.14** below.

Table 4.14 Air quality monitoring Station for Contract no. HK/2012/08

Station	Description
CMA5b	Pedestrian Plaza

Reporting month of March 2017

- 4.3.29 One 24hr TSP limit level exceedance was recorded at CMA5b on 02 March 2017.
- 4.3.30 Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition was implemented and no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.
- 4.3.31 Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedance were recorded at CMA5b on 03 March 2017.
- 4.3.32 Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition was implemented and no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.

Reporting month of April 2017

4.3.33 No exceedance was recorded in the reporting month.

Reporting month of May 2017

4.3.34 No exceedance was recorded in the reporting month.

4.3.35 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in [Appendix 4.3](#).

Contract no. HY/2010/08 – Central-Wanchai Bypass –Wanchai Bypass Tunnel (Slip Road 8 Section) under FEP-09/364/2009/B

4.3.36 The commencement of construction works for Contract no. HY/2010/08 under FEP-09/364/2009/B was on July 2014. Air quality monitoring was commenced on 14 July 2011. The proposed division of air quality monitoring stations are summarized in **Table 4.15** below.

Table 4.15 Air quality monitoring Station for Contract no. HY/2010/08

Station	Description
CMA3a	CWB PRE Site Office

4.3.37 No action or limit level exceedance was recorded in the reporting period.

4.3.38 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in [Appendix 4.3](#).

Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning

4.3.39 Air quality monitoring for the Central Interchange works under contract no. HY/2011/08 was commenced on 21 April 2011. The proposed division of air quality monitoring stations are summarized in **Table 4.16** below.

Table 4.16 Air quality monitoring Stations for Contract no. HY/2011/08

Station	Description
MA1e	International Finance Centre (Eastern End of Podium)
MA1w	International Finance Centre (Western End of Podium)
CMA1b	Oil Street Site Office
CMA2a	Causeway Bay Community Centre

4.3.40 No action or limit level exceedance was recorded in the reporting period.



- 4.3.41 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in [Appendix 4.3.](#)

4.4. Waste Monitoring Results

Contract no. HK/2009/01 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Hong Kong Convention and Exhibition Centre - Tunnel Works under FEP-02/364/2009

- 4.4.1. Inert and non-inert C&D waste was disposed of in this reporting period. Details of the waste flow table are summarized in **Table 4.17**.

Table 4.17 Details of Waste Disposal for Contract no. HK/2009/01

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date. m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	57.83	107983.85	TKO137, TM38
Inert C&D materials recycled	Nil	98512.03	N/A
Non-inert C&D materials disposed	48.08	5279.06	SENT Landfill
Non-inert C&D materials recycled	Nil	1285746	N/A
Chemical waste disposed	Nil	10400	Kwun Kee (Chemical Waste Collector)
Marine Sediment (Type 1- Open Seas Disposal), m3	Nil	11527	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m3	Nil	16261	East of Cha Chau South Brothers

Contract no. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East (CWB Tunnel) under FEP-01/364/2009

- 4.4.2. Inert and non-inert C&D waste were disposed of in this reporting period. Details of the waste flow table are summarized in **Table 4.18**.

Table 4.18 Details of Waste Disposal for Contract no. HK/2009/02

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date. m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	563	522166.412	TKO137, TM 38
Inert C&D materials recycled	Nil	46520	WCR2
Non-inert C&D materials disposed	337	4416.317	SENT Landfill
Non-inert C&D materials recycled	Nil	N/A	N/A
Chemical waste disposed	Nil	17718	N/A

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date. m ³	Disposal / Dumping Grounds
Marine Sediment (Type 1 – Open Sea Disposal) , m ³	Nil	65663	South Cheung Chau

Contract no. HY/2009/18 - Central - Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- 4.4.3. Inert and non-inert C&D waste was disposed of in this reporting period. Details of the waste flow table are summarized in **Table 4.19**.

Table 4.19 Details of Waste Disposal for Contract no. HY/2009/18

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date. m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	427.1	1415282.75	T.K.O. 137
Inert C&D materials recycled	Nil	58787.05	N/A
Non-inert C&D materials disposed	17.12	4366.62	SENT Landfill
Non-inert C&D materials recycled (tonnes)	Nil	878.37	N/A
Chemical waste disposed	Nil	6772	N/A

Remarks: The cumulative amount of inert C&D material disposed has been updated in the reporting period.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) under FEP-06/364/2009/A

- 4.4.4. Inert and non-inert C&D waste was disposed of in this reporting period. Details of the waste flow table are summarized in **Table 4.20**.

Table 4.20 Details of Waste Disposal for Contract no. HY/2009/15

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date. m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	Nil Nil	625200.92 245453.3	Tuen Mun Area 38 TKO137 FB
Inert C&D materials recycled	Nil	358660.77	HY/2009/11, ex-PCWA TS4
Non-inert C&D materials disposed	0.81 Nil	4673.91 1.58	SENT Landfill WENT Landfill
Non-inert C&D materials recycled	Nil	5496446.2	Xun Xiang Metal ware Skylight Recycle (paper)
Chemical waste disposed	Nil	22755	Dunwell Group

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date. m ³	Disposal / Dumping Grounds
Marine Sediment (Type1-Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal), m ³	Nil	5684	South of the Brothers

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

- 4.4.5. Inert C&D materials was recycled non-inert C&D waste was disposed of in this reporting period. Details of the waste flow table are summarized in **Table 4.21**.

Table 4.21 Details of Waste Disposal for Contract no. HY/2009/19

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date. m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	13189.08	686993.92	N/A
Inert C&D materials recycled	Nil	82349.7	N/A
Non-inert C&D materials disposed	341.57	5882.89	SENT Landfill
Non-inert C&D materials recycled	Nil	565.63	N/A
Chemical waste disposed	Nil	10.15	N/A
Marine Sediment (Tunnel) (Type 1- Open Sea Disposal), m ³	Nil	20556	South of Cheung Chau
Marine Sediment (Tunnel) (Type 1- Open Sea Disposal (Dedicated Sites) & Type 2 – Confined Marine Disposal), m ³	Nil	30751	East of Sha Chau

Contract no. HK/2012/08 Wan Chai Development Phase II - Central-Wan Chai Bypass at Wan Chai West under FEP-09/364/2009/B and FEP-12/364/2009/D

- 4.4.6. No inert and Non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 4.22**.

Table 4.22 Details of Waste Disposal for Contract no. HK/2012/08

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	973 Nil	183078 116668	TKO137 TM38
Inert C&D materials recycled	Nil	Nil	N/A
Non-inert C&D materials disposed	1835	7637	N/A
Non-inert C&D materials recycled	NIL	Nil	N/A
Chemical waste disposed	NIL	Nil	N/A
Marine Sediment (Type 1) Disposal, m ³	Nil	3145	South of Cheung Chau/ South of Brothers

Remarks: The quantity of inert C&D material disposed, recycled, non-inert C&D material disposed, recycled are reported up to calendar month on 31 February 2017. The cumulative amount of inert C&D material disposed in the reporting quarter have been clarified.

Contract no. HY/2010/08 Central – Wan Chai Bypass (CWB) – Tunnel (Slip Road 8) under FEP-10/364/2009/B

- 4.4.7. No inert and Non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 4.23**.

Table 4.23 Details of Waste Disposal for Contract no. HY/2010/08

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	5795.67 Nil Nil 172.46	583935.84 262656.6 82911.8 72670.15	TM 38 WENT SENT TKO area 137
Inert C&D materials recycled	Nil	Nil	Nil
Non-inert C&D materials disposed	775.5	4543.03	SENT
Non-inert C&D materials recycled	Nil	Nil	Nil
Chemical waste disposed	Nil	979	Nil
Type 1 – Open Sea Disposal	Nil	16368.4	East Sha Chau/ South Brothers Island
Type 2 – Confined Marine disposal	Nil	549.2	East Sha Chau

Remarks: The cumulative amount of non-inert C&D material disposed has been clarified in the reporting quarter.

Contract no. HY/2011/08 Central –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009B

- 4.4.8. No inert and Non-inert C&D wastes were disposed of in this reporting month. Details of the waste flow table are summarized in **Table 4.24**.

Table 4.24 Details of Waste Disposal for Contract no. HY/2011/08

Waste Type*	Quantity this quarter, m ³	Cumulative-to-Date, m ³	Disposal / Dumping Grounds
Inert C&D materials disposed	35.97	681.3	Nil
Inert C&D materials recycled	Nil	Nil	Nil
Non-inert C&D materials disposed	677.16	2626.05	Nil
Non-inert C&D materials recycled	Nil	31.72	Nil
Chemical waste disposed(kg)	Nil	3800	Nil

5. COMPLIANCE AUDIT

5.0.1. The Event Action Plan for construction noise and air quality are presented in [Appendix 5.1](#).

5.1. Noise Monitoring

Contract no. HY/2009/18 - Central - Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

5.1.1. No action or limit level exceedance was recorded in this reporting quarter.

Contract no. HK/2009/01 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Hong Kong Convention and Exhibition Centre - Tunnel Works

[Reporting Month of March 2017](#)

5.1.2. No action or limit level exceedance was recorded in this reporting quarter.

[Reporting Month of April 2017](#)

5.1.3. No action or limit level exceedance was recorded in this reporting quarter.

[Reporting Month of May 2017](#)

5.1.4. Two limit level exceedances were recorded at M1a – Footbridge for Ex-Harbour Road Sports Centre on 16 and 25 May 2017 in the reporting month.

5.1.5. No Construction works was conducted under Contract HK/2009/01 around the monitoring station on 16 and 25 May 2017, non WDII-CWB Projects breaking and drilling works was observed on 16 May 2017 and non WDII-CWB Project bored piling works was conducted on 25 May 2017 during monitoring period and observed as the major noise contribution. Hence, the exceedances were considered as non-Project related.

Contract no. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East (CWB Tunnel)

[Reporting Month of March 2017](#)

5.1.6. No action or limit level exceedance was recorded in this reporting quarter.

[Reporting Month of April 2017](#)

5.1.7. No action or limit level exceedance was recorded in this reporting quarter.

[Reporting Month of May 2017](#)

5.1.8. Two limit level exceedances were recorded at M1a – Footbridge for Ex-Harbour Road Sports Centre on 16 and 25 May 2017 in the reporting month.

- 5.1.9. Despite rebar fixing, and formwork fixing works was conducted on 16 May 2017 and rebar fixing was conducted on 25 May 2017 under Contract HK/2009/02, non WDII-CWB Projects breaking and drilling works was observed on 16 May 2017 and non WDII-CWB Project bored pilling works was conducted on 25 May 2017 during monitoring period and observed as the major noise contribution. Hence, the exceedances were considered as non-Project related.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) FEP-06/364/2009/A

- 5.1.10. No action or limit level exceedance was recorded in this reporting quarter.

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

Reporting Month of March 2017

- 6.1.1. No exceedance was recorded in the reporting month.

Reporting Month of April 2017

- 6.1.2. Three limit level exceedances were recorded at M6 – Hk Baptist Church Henrietta Secondary School on 03, 10 and 26 April 2017 in the reporting month.

- 6.1.3. Traffic noise was observed during monitoring on 03, 10 and 26 April 2017 and were considered as the major noise contribution. As such, the limit level exceedance was concluded as non-project related.

- 6.1.4. One limit level exceedance was recorded at M5b – City Garden on 18 April 2017 in the reporting month.

- 6.1.5. Starter bar fixing works and breaking works at marine pier under Contract HY/2009/19 was conducted during the measurement on 18 April 2017, it was observed that breaking operation was the major noise contribution during measurement. It is concluded that the exceedance was Project related and the contractor was requested to submit a proposal for remediation measures following the Event and Action Plan. Actions from the remediation plan including i) Closing the opening of the temporary noise barrier ii) provide physical wrapping of breaker to dampen noise emission and iii) conduct breaking works intermittently were implemented by the Contractor and no further exceedance was recorded upon implementation of the remedial actions.

Reporting Month of May 2017

- 6.1.6. No exceedance was recorded in the reporting month.

Contract no. HY/2010/08 – Central-Wanchai Bypass – Tunnel (Slip Road 8 Section) under FEP-10/364/2009/B

- 5.1.11. No action of limit level exceedance was recorded in the reporting quarter

Contract no. HY/2011/08 Central –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009B

- 5.1.12. No action of limit level exceedance was recorded in the reporting quarter.

5.2. Air quality monitoring

Contract no. HY/2009/18 - Central - Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

- 5.2.1. No action or limit level exceedance was recorded in the reporting quarter.

Contract no. HK/2009/01 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Hong Kong Convention and Exhibition Centre - Tunnel Works

Reporting month of March 2017

- 5.2.2. One 24hr TSP limit level exceedance was recorded at CMA5b on 02 March 2017.

- 5.2.3. No construction works was undertaken on 02 March 2017 around Pedestrian Plaza under Contract HK/2009/01, no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.

- 5.2.4. Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedance were recorded at CMA5b on 03 March 2017.

- 5.2.5. No construction works was undertaken on 03 March 2017 around Pedestrian Plaza under Contract HK/2009/01, no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.

Reporting month of April 2017

- 5.2.6. No action or limit level exceedance was recorded in the reporting quarter.

Reporting month of May 2017

- 5.2.7. No action or limit level exceedance was recorded in the reporting quarter.

Contract nos. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East (CWB Tunnel)

Reporting month of March 2017

- 5.2.8. One 1hr TSP limit level exceedance was recorded at CMA4a on 03 March 2017.

- 5.2.9. Despite backfilling works at Portion 3&4 and tunnel structure works at Portion 5 were conducted on 03 March 2017 on the monitoring date around the monitoring station under Contractor of HK/2009/02, dust suppression measure including covering of stockpile and

watering for haul road and during loading and unloading of material were implemented by the Contractor and no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and the observed renovation works next to the monitoring station.

Reporting month of April 2017

- 5.2.10. No exceedance was recorded in the reporting month.

Reporting month of May 2017

- 5.2.11. No exceedance was recorded in the reporting month.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section) FEP-06/364/2009/A

- 5.2.12. No action or limit level exceedance was recorded in the reporting quarter.

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

Reporting month of March 2017

- 5.2.13. One 1hr TSP limit level exceedance was recorded at CMA1b on 27 March 2017.

- 5.2.14. No construction works was undertaken under Contract HY/2009/19 on the monitoring date at around Oil Street Site Office while the haul road around the concerned location was observed maintained in dampened condition and no particular observation regarding air quality impact was observed during sampling. In view of the above, the limit level exceedance was considered to be non-project related and contributed by local ambient condition.

Reporting month of April 2017

- 5.2.15. No exceedance was recorded in the reporting month.

Reporting month of May 2017

- 5.2.16. No exceedance was recorded in the reporting month.

Contract no. HK/2012/08 Wan Chai Development Phase II - Central-Wan Chai Bypass at Wan Chai West under FEP-09/364/2009/B and FEP-12/364/2009/D

Reporting month of March 2017

- 5.2.17. One 24hr TSP limit level exceedance was recorded at CMA5b on 02 March 2017.

- 5.2.18. Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition was implemented and no particular

- observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.
- 5.2.19. Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedance were recorded at CMA5b on 03 March 2017.
- 5.2.20. Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition was implemented and no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.
- Reporting month of April 2017
- 5.2.21. No exceedance was recorded in the reporting month.
- Reporting month of May 2017
- 5.2.22. No exceedance was recorded in the reporting month.
- Contract no. HY/2010/08 – Central-Wanchai Bypass – Tunnel (Slip Road 8 Section) under FEP-10/364/2009/B
- 5.2.23. No exceedance was recorded in the reporting quarter
- Contract no. HY/2011/08 Central –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009B
- Reporting month of March 2017
- 5.2.24. One 1hr TSP limit level exceedance was recorded at CMA1b on 27 March 2017.
- 5.2.25. Concrete and bar fixing works was undertaken under Contract HY/2011/08 on the monitoring date at around Oil Street Site Office while regular water spraying on ground was generally implemented by the Contractor and no particular observation regarding air quality impact was observed during sampling. In view of the above, the limit level exceedance was considered to be non-project related and contributed by local ambient condition.
- 5.2.26. One 24hr TSP limit level exceedance was recorded at CMA5b on 02 March 2017.
- 5.2.27. Despite ground paving by concrete and plant mobilization were undertaken on the monitoring date at the Central Ventilation Building under Contractor of HY/2011/08, no particular observation regarding air quality impact was observed during sampling. The exceedance was

- considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.
- 5.2.28. Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedance were recorded at CMA5b on 03 March 2017.
- 5.2.29. Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition was implemented and no particular observation regarding air quality impact was observed during sampling. The exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station.
- Reporting month of April 2017
- 5.2.30. No exceedance was recorded in the reporting month.
- Reporting month of May 2017
- 5.2.31. No exceedance was recorded in the reporting month.
- 5.3. Real Time Noise Monitoring**
- Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D
- Reporting month of March 2017
- 5.3.1 No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 5.3.2 Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre on 27, 28 February and 01, 02 and 03 March 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, sheet piling, pre bored drilling and breaking works were conducted on 27, 28 February and 01, 02 and 03 March 2017 and temporary noise barrier was generally implemented and breaking works was conducted behind physical building structure while building construction works with breaking and hammering works under non-CWB private development site at Oil Street was conducted at the building level adjacent to the noise monitoring station and were considered as the major noise contribution across the monitoring period. As such, the exceedances were considered as non-Project related.
- 5.3.3 No limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School in the reporting month.
- 5.3.4 No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre in the reporting month.

Reporting month of April 2017

- 5.3.5 No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 5.3.6 No limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded in the reporting month.
- 5.3.7 No limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School in the reporting month.
- 5.3.8 Limit level exceedance was recorded at RTN4- Causeway Bay Community Centre were recorded on 20 and 21 April 2017 in the reporting month. After checking with Contractor HY/2009/19, no construction works activity was conducted on 20 and 21 April 2017 during the monitoring period while non - CWB breaking was observed conducted on the monitoring dates immediately next to the monitoring station. As such, the exceedances were concluded as non-Project related.

Reporting month of May 2017

- 5.3.9 No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 5.3.10 Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded on 24 May 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, despite sheet piling works was conducted during the monitoring period, adverse weather condition under Red Rainstorm Warning Signal was considered as the major noise contribution during monitoring and hence the exceedance was concluded as non-Project related.
- 5.3.11 Limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School on 10 and 24 May 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, no construction works were conducted on 10 and 24 May 2017 around the monitoring location during the concerned period and hence the exceedances were considered to be non-Project related and potentially related to the traffic on 10 May 2017 and the adverse weather under Red Rainstorm Warning Signal on 24 May 2017.
- 5.3.12 No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre was recorded in the reporting month.

Contract no. HY/2011/08 Central –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009B

Reporting month of March 2017

- 5.3.13 No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 5.3.14 Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre on 27, 28 February and 01, 02 and 03 March 2017 during daytime in the reporting month. After checking with Contractor of HY/2011/08, formworks, bar fixing and concreting works were conducted on 27, 28 February and 01, 02 and 03 March 2017 and no particular noise was considered for the works while building construction works with breaking and hammering works under non-CWB private development site at Oil Street was conducted at the building level adjacent to the noise monitoring station and were considered as the major noise contribution across the monitoring period. As such, the exceedances were considered as non-Project related.
- 5.3.15 No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.

Reporting month of April 2017

- 5.3.16 No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 5.3.17 No limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded in the reporting month.
- 5.3.18 Limit level exceedance was recorded at RTN4- Causeway Bay Community Centre were recorded on 20 and 21 April 2017 in the reporting month. After checking with Contractor HY/2011/08, no construction works activity was conducted on 20 and 21 April 2017 during the monitoring period while non - CWB breaking was observed conducted on the monitoring dates immediately next to the monitoring station. As such, the exceedances were concluded as non-Project related.

Reporting month of May 2017

- 5.3.19 No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 5.3.20 Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded on 24 May 2017 during daytime in the reporting month. After checking with Contractor of HY/2011/08, no construction works was conducted during the monitoring period and adverse weather condition under Red Rainstorm Warning Signal was considered as the major noise contribution during monitoring and hence the exceedance was concluded as non-Project related.
- 5.3.21 No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre were recorded in the reporting month.

5.4. Site Audit

- 5.4.1. There was no non-compliance from the site audits in the reporting period. During environmental site inspections conducted during the reporting quarter, minor deficiencies were noted. However, the Contractor rectified all deficiencies after receipt of notification.

5.5. Review of the Reasons for and the Implications of Non-compliance

- 5.5.1 One project related limit level exceedance was recorded at M5b – City Garden on 18 April 2017 in the reporting month. The exceedance was concluded as related to the breaking works at marine pier under Contract HY/2009/19 in the reporting quarter.
- 5.5.2 According to RSS site information, non-compliance with Construction Noise Permits condition under Noise Control Ordinance under Contract HK/2009/02 were observed by RSS team on 09, 10, 12 and 21 May 2017 at Wanchai Area with potential noise concern during restricted hours in the reporting quarter.

5.6. Summary of action taken in the event of and follow-up on non-compliance

- 5.6.1 Starter bar fixing works and breaking works at marine pier under Contract HY/2009/19 was conducted during the measurement on 18 April 2017, it was observed that breaking operation was the major noise contribution during measurement. It is concluded that the exceedance was Project related.
- 5.6.2 The contractor was requested to submit a proposal for remediation measures following the Event and Action Plan. Actions from the remediation plan including i) Closing the opening of the temporary noise barrier ii) provide physical wrapping of breaker to dampen noise emission and iii) conduct breaking works intermittently were implemented by the Contractor and no further exceedance was recorded upon implementation of the remedial actions.
- 5.6.3 In response to the information provided by the RSS, relevant investigation report(s) by the Environmental Team reviewed by the Independent Environmental Checker were submitted to the EPD. Ad-hoc site inspection for restricted hours operations on Noise Control Ordinance were conducted by the Environmental Team on 13, 19 and 26 May 2017 to check the Contractor HK/2009/02 Construction Noise Permit Compliance. Subsequently, two Construction Noise Permits, GW-RS0334-17 and GW-RS1297-16 were cancelled by the Authority on 26 May 2017.
- 5.6.4 The Contractor of HK/2009/02 was requested to implement remedial actions to rectify the environmental concern. The improvement plan for restricted hours operations control were provided by the Contractor of HK/2009/02 to the ET/IEC/RSS/ EPD for follow up on Contractor compliance during restrict hours.

6. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

6.0.1 Five environmental complaints were received in the reporting quarter.

6.0.2 First ICC complaint referred by RSS was received by ET on 27 February 2017 (CASE#2-3521097579). The complainant reported that noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.

ET confirmed with the Resident Site Staff that no construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017.

No construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017.

Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

6.0.3 Second ICC complaint referred by RSS was received by ET on 06 March 2017 (CASE#2-3576157538). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.

The ICC complaint was subsequently referred to the EPD. EPD subsequently refer the same complaint case to the ET on 14 March 2017 (EPD Ref: H05/RS/0006240-17). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.

ET confirmed with the Resident Site Staff that no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 no. of loader were in operation below ground level.

According to the information confirmed by RSS, no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5

(West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 loader were in operation below ground level. Relevant Construction Noise Permit GW-RS1305-16 was in place.

Nevertheless, in view of the public concern, the Contractor of HK/2009/02 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HK/2009/02 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

- 6.0.4 Third ICC complaint referred by RSS was received by ET on 13 March 2017 (CASE#2-3603182890). The complainant reported that noise was emanated from the construction Site at Victoria Park from 2300hrs to 2400hrs on 10 March 2017 and caused nuisance to nearby residents.

ET confirmed with the Resident Site Staff that no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.

Based on the information provided by the RSS, no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.

Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

- 6.0.5 Forth EPD complaint was referred to the ET on 18 May 2017 (CASE Ref: H05/RS/00014415-17(14448-17). The complainant reported that construction work was found on 10 May 2017 (~03:52) that caused noise nuisance. According to the photos provided by the complainant lorry mounted concrete pump were used. According to the information provided by the IEC on 11 May 2017 and 15 May 2017, it was alleged that the concreting work under Contract No. HK/2009/02 was carried out for the Central-Wan Chai Bypass Top Slab Bay 6 during night time on 09 May 2017 and early morning on 10 May 2017 (between 11:00pm on 09 May 2017 and about 04:00 a.m. on 10 May 2017) with 3 pump trucks, 10 vibrating pokers, 9 concrete trucks and 2 generators in operation. The concreting works under Contract No. CEDD HK/2009/02 was also carried out for the Central – Wan Chai Bypass Bay 10A OHVS Slab after 23:00 on 12 May 2017 (after 23:00) with 1 Pump truck, 2 vibrating pokers, 1 concrete trucks and 3 generators in operation.

ET confirmed with the Resident Site Staff that 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from

2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017. 2 nos. of vibratory pokers, 1 no. of concrete truck, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017.

According to the RSS site information, 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generator were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 11 May 2017, ad-hoc inspection was conducted by the Environmental Team on 13 May 2017 around 00:40 hrs. No construction operation and no PME deployment was observed at the time of inspection.

According to the RSS site information, 2 nos. of vibratory pokers, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017 and could not comply with the item 3a - PME requirement under Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 15 May 2017, ad-hoc inspection was conducted by the Environmental Team on 19 May 2017 around 22:20hrs. 2 nos. of concrete truck, 1 no. of concrete pump truck were observed in operation at the time of inspection and relevant CNP GW-RS0334-17 was in place.

Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Contractor of HK/2009/02 is also recommended to provide briefing and training session to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/2009/02 during restricted hours and report relevant findings, if any, accordingly.

- 6.0.6 Fifth EPD complaint was referred to the ET on 25 May 2017 (CASE Ref: N/A). The complainant reported that concreting works under Contract No. CEDD HK/2009/02 was carried out with crawler cranes, 10-12 vibratory pokers, and 7 concrete lorry mixers in the morning on 21 May 2017 without a valid CNP. Also, at 15:30 on 21 May 2017, 9 vibratory pokers and 7 concrete lorry mixers were observed in operation. These works were suspected to contravene the Noise Control Ordinance (NCO).

ET confirmed with the Resident Site Staff that 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017. 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs on 21 May 2017. 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 7 nos. of concreting trucks were operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017.

According to the RSS site information, the following PME were operated on 21 May 2017, i) 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs; ii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs; iii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017; iv) 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs; v) 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs ; 7 nos. of concreting trucks were operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS334-17.

EPD notification on the cancellation of the Construction Noise Permits GW-RS0334-17 and Construction Noise Permit GW-RS1297-16 was received by the Environmental Team on 26 May 2017. Ad hoc inspection was conducted by the Environmental Team on 26 May 2017 around 2230hrs and on 28 May 2017 around 1520hrs and no construction works and no operation of PME was observed at the concerned site Portion 5 at the time of inspections. Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Contractor of HK/2009/02 is also recommended to provide briefing and training session to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/2009/02 during restricted hours and report relevant findings, if any, accordingly.

- 6.0.7 The details of cumulative complaint log and summary of complaints are presented in **Appendix 6.1**.
- 6.0.8 Two Summons to Defendant (Case No. ESS38444/2016 and Case No.ESS38443/2016) were issued to the Contractor(s) under Contract HY/2009/19 on 06 October 2016 regarding the case against (Regulations 4(1) and 4(2) of the Air Pollution Control (Construction Dust) Regulation made under section 43 of the Air Pollution Control Ordinance, Cap311 were notified to the Environmental Team on 31 March 2017.

- 6.0.9 The offence under the two Summons to Defendant (Case No. ESS38444/2016 and Case No. ESS38443/2016) were issued to the Contractor(s) under Contract HY/2009/19 on 06 October 2016 regarding the case against (Regulations 4(1) and 4(2) of the Air Pollution Control (Construction Dust) Regulation made under section 43 of the Air Pollution Control Ordinance, Cap311 were convicted on 03 April 2017.
- 6.0.10 Two Summons to Defendant (Case No. ESS40680/2016 and Case No. ESS40679/2016) were issued to the Contractor(s) under Contract HY/2009/19 on 25 October 2016 regarding the case against Section 6(1)(b) and 6(5), Noise Control Ordinance Cap 400 were convicted on 04 May 2017.
- 6.0.11 Cumulative statistic on complaints and successful prosecutions are summarized in **Table 6.1** and **Table 6.2** respectively.

Table 6.1 Cumulative Statistics on Complaints

Reporting Period	No. of Complaints
Commencement of Works up to last reporting quarter	75
March 2017 to May 2017	5
Project-to-Date	80

Table 6.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this quarter (Offence Date)	Cumulative No. Project-to-Date
Air	-	1 (05 April 2016)	1
Noise	-	1 (24 April 2016)	1
Waste	-	0	0
Total	-	2	2

7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS

- 7.0.1. According to Condition 3.4 of the EP-364/2009/E, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) and Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel).
- 7.0.2. According to the Final EM&A Report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011. As such, it is considered that there were no cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) undertaken by contractor HK12/02 in the reporting period.
- 7.0.3. According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area include road and drain works, backfilling works and reinstatement of Culvert and Cooling mains were performed in May 2017 reporting month. As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were, road and drains construction, tunnel construction, backfilling works, road and drains works at Wan Chai West and Wan Chai East. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were drainage works and ventilation building construction at Central; backfilling and temporary reclamation removal works at Causeway Bay, road works and side wall construction at Victoria Park; bridge construction, piling works and tunnel works at North Point area in the reporting month. In addition, other non-Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects was observed undertaken at Wan Chai North and North Point area.
- 7.0.5. No significant air impact from construction activities was anticipated in the reporting month. Besides, no project related exceedance was recorded during the air and noise environmental monitoring events in the reporting month. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) was insignificant.

8. CONCLUSION

- 8.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.

Air quality monitoring

- 8.0.2. One 1hr TSP limit level exceedance was recorded at CMA1b- Oil Street Site Office on 27 March 2017 in the reporting month. The exceedance was concluded to be non-Project related.
- 8.0.3. One 1hr TSP limit level exceedances were recorded at CMA4a – Society for the Prevention of Cruelty to Animals on 03 March 2017 in the reporting month. The exceedance was concluded to be non-Project related.
- 8.0.4. One 24hr TSP limit level exceedance was recorded at CMA5b – Pedestrian Plaza on 02 March 2017 in the reporting month. The exceedance was concluded to be non-Project related.
- 8.0.5. Two 1hr TSP action level exceedances and one 1hr TSP limit level exceedance were recorded at CMA5b –Pedestrian Plaza on 03 March 2017 in the reporting month. The exceedances were concluded to be non-Project related.

Noise monitoring

- 8.0.6. Three limit level exceedance were recorded at M6 – HK Baptist Church Henrietta Secondary School on 03, 10 and 26 April 2017 in the reporting month. The exceedances were concluded as non Project related.
- 8.0.7. One limit level exceedance was recorded at M5b – City Garden on 18 April 2017. The exceedance was concluded as Project related.
- 8.0.8. Two limit level exceedances were recorded at M1a – Footbridge for Ex-Harbor Road Sports Centre on 16 and 25 May 2017 in the reporting month. The exceedances were concluded as non Project related.

Real time noise monitoring

Reporting month of March 2017

- 8.0.9. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 8.0.10. Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre on 27, 28 February and 01, 02 and 03 March 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, sheet piling, pre bored drilling and breaking works were conducted on 27, 28 February and 01, 02 and 03 March 2017 and temporary noise barrier was generally implemented and breaking works was conducted behind physical building structure while building construction works with breaking and hammering works under non-CWB private development site at Oil Street was conducted at the building level adjacent to the noise monitoring station and were considered as the major noise contribution across the monitoring period. As such, the exceedances were considered as non-Project related.
- 8.0.11. After checking with Contractor of HY/2011/08, formworks, bar fixing and concreting works were conducted on 27, 28 February and 01, 02 and 03 March 2017 and no particular noise was considered for the works while building construction works with breaking and hammering works under non-CWB private development site at Oil Street was conducted at the building level adjacent to the noise monitoring station and were considered as the major noise contribution across the monitoring period. As such, the exceedances were considered as non-Project related.
- 8.0.12. No limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School in the reporting month.
- 8.0.13. No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre in the reporting month.

Reporting month of April 2017

- 8.0.14. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 8.0.15. No limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded in the reporting month.
- 8.0.16. No limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School in the reporting month.
- 8.0.17. Limit level exceedance was recorded at RTN4- Causeway Bay Community Centre were recorded on 20 and 21 April 2017 in the reporting month. After checking with Contractor HY/2009/19, no construction works activity was conducted on 20 and 21 April 2017 during the monitoring period while non - CWB breaking was observed conducted on the monitoring

dates immediately next to the monitoring station. As such, the exceedances were concluded as non-Project related. After checking with Contractor of HY/2011/08, formwork and bar fixing works were conducted at the Administration building area on 16, 18, 19, 20, 21, 23 and 24 and no particular noise was considered and no construction works was conducted on 25 January 2017. Nevertheless, Non CWB Project building construction works with drilling and breaking works opposite to the monitoring station at Oil Street were observed across January 2017 and observed as the major noise contribution throughout the monitoring period. In view of the above, the exceedances were considered as non-Project related.

- 8.0.18. After checking with Contractor HY/2011/08, no construction works activity was conducted on 20 and 21 April 2017 during the monitoring period while non - CWB breaking was observed conducted on the monitoring dates immediately next to the monitoring station. As such, the exceedances were concluded as non-Project related.

Reporting month of May 2017

- 8.0.19. No limit level exceedance was recorded at RTN1-FEHD Hong Kong Transport Section Whitfield Depot was recorded in the reporting month.
- 8.0.20. Limit level exceedances were recorded at RTN2a- Hong Kong Electric Centre was recorded on 24 May 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, despite sheet piling works was conducted during the monitoring period, adverse weather condition under Red Rainstorm Warning Signal was considered as the major noise contribution during monitoring and hence the exceedance was concluded as non-Project related.
- 8.0.21. After checking with Contractor of HY/2011/08, no construction works was conducted during the monitoring period and adverse weather condition under Red Rainstorm Warning Signal was considered as the major noise contribution during monitoring and hence the exceedance was concluded as non-Project related.
- 8.0.22. Limit level exceedances were recorded at RTN3- Yu Lee Mo Fan Memorial School on 10 and 24 May 2017 during daytime in the reporting month. After checking with Contractor of HY/2009/19, no construction works were conducted on 10 and 24 May 2017 around the monitoring location during the concerned period and hence the exceedances were considered to be non-Project related and potentially related to the traffic on 10 May 2017 and the adverse weather under Red Rainstorm Warning Signal on 24 May 2017.
- 8.0.23. No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre was recorded in the reporting month.

Environmental Complaints

8.0.24. Five environmental complaints were received in the reporting quarter.

8.0.25. First ICC complaint referred by RSS was received by ET on 27 February 2017 (CASE#2-3521097579). The complainant reported that noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.

ET confirmed with the Resident Site Staff that no construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017.

No construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017.

Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

8.0.26. Second ICC complaint referred by RSS was received by ET on 06 March 2017 (CASE#2-3576157538). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.

The ICC complaint was subsequently referred to the EPD. EPD subsequently refer the same complaint case to the ET on 14 March 2017 (EPD Ref: H05/RS/0006240-17). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.

ET confirmed with the Resident Site Staff that no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 no. of loader were in operation below ground level.

According to the information confirmed by RSS, no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to

1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 loader were in operation below ground level. Relevant Construction Noise Permit GW-RS1305-16 was in place.

Nevertheless, in view of the public concern, the Contractor of HK/2009/02 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HK/2009/02 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

- 8.0.27. Third ICC complaint referred by RSS was received by ET on 13 March 2017 (CASE#2-3603182890). The complainant reported that noise was emanated from the construction Site at Victoria Park from 2300hrs to 2400hrs on 10 March 2017 and caused nuisance to nearby residents.

ET confirmed with the Resident Site Staff that no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.

Based on the information provided by the RSS, no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.

Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.

- 8.0.28. Forth EPD complaint was referred to the ET on 18 May 2017 (CASE Ref: H05/RS/00014415-17(14448-17). The complainant reported that construction work was found on 10 May 2017 (~03:52) that caused noise nuisance. According to the photos provided by the complainant lorry mounted concrete pump were used. According to the information provided by the IEC on 11 May 2017 and 15 May 2017, it was alleged that the concreting work under Contract No. HK/2009/02 was carried out for the Central-Wan Chai Bypass Top Slab Bay 6 during night time on 09 May 2017 and early morning on 10 May 2017 (between 11:00pm on 09 May 2017 and about 04:00 a.m. on 10 May 2017) with 3 pump trucks, 10 vibrating pokers, 9 concrete trucks and 2 generators in operation. The concreting works under Contract No. CEDD HK/2009/02 was also carried out for the Central – Wan Chai Bypass Bay 10A OHVS Slab after 23:00 on 12 May 2017 (after 23:00) with 1 Pump truck, 2 vibrating pokers, 1 concrete trucks and 3 generators in operation.

ET confirmed with the Resident Site Staff that 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from

2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017. 2 nos. of vibratory pokers, 1 no. of concrete truck, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017.

According to the RSS site information, 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generator were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 11 May 2017, ad-hoc inspection was conducted by the Environmental Team on 13 May 2017 around 00:40 hrs. No construction operation and no PME deployment was observed at the time of inspection.

According to the RSS site information, 2 nos. of vibratory pokers, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017 and could not comply with the item 3a - PME requirement under Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 15 May 2017, ad-hoc inspection was conducted by the Environmental Team on 19 May 2017 around 22:20hrs. 2 nos. of concrete truck, 1 no. of concrete pump truck were observed in operation at the time of inspection and relevant CNP GW-RS0334-17 was in place.

Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Contractor of HK/2009/02 is also recommended to provide briefing and training session to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/2009/02 during restricted hours and report relevant findings, if any, accordingly.

- 8.0.29. Fifth EPD complaint was referred to the ET on 25 May 2017 (CASE Ref: N/A). The complainant reported that concreting works under Contract No. CEDD HK/2009/02 was carried out with crawler cranes, 10-12 vibratory pokers, and 7 concrete lorry mixers in the morning on 21 May 2017 without a valid CNP. Also, at 15:30 on 21 May 2017, 9 vibratory pokers and 7 concrete lorry mixers were observed in operation. These works were suspected to contravene the Noise Control Ordinance (NCO).

ET confirmed with the Resident Site Staff that 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017. 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs on 21 May 2017. 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 7 nos. of concreting trucks were operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017.

According to the RSS site information, the following PME's were operated on 21 May 2017, i) 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs; ii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs; iii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017; iv) 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs; v) 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs ; 7 nos. of concreting trucks were operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS334-17.


EPD notification on the cancellation of the Construction Noise Permits GW-RS0334-17 and Construction Noise Permit GW-RS1297-16 was received by the Environmental Team on 26 May 2017. Ad hoc inspection was conducted by the Environmental Team on 26 May 2017 around 2230hrs and on 28 May 2017 around 1520hrs and no construction works and no operation of PME was observed at the concerned site Portion 5 at the time of inspections. Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PME's deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Contractor of HK/2009/02 is also recommended to provide briefing and training session to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/2009/02 during restricted hours and report relevant findings, if any, accordingly.

8.0.30. The construction programmes of individual contracts are provided in **Appendix 8.1**.



Figure 2.1

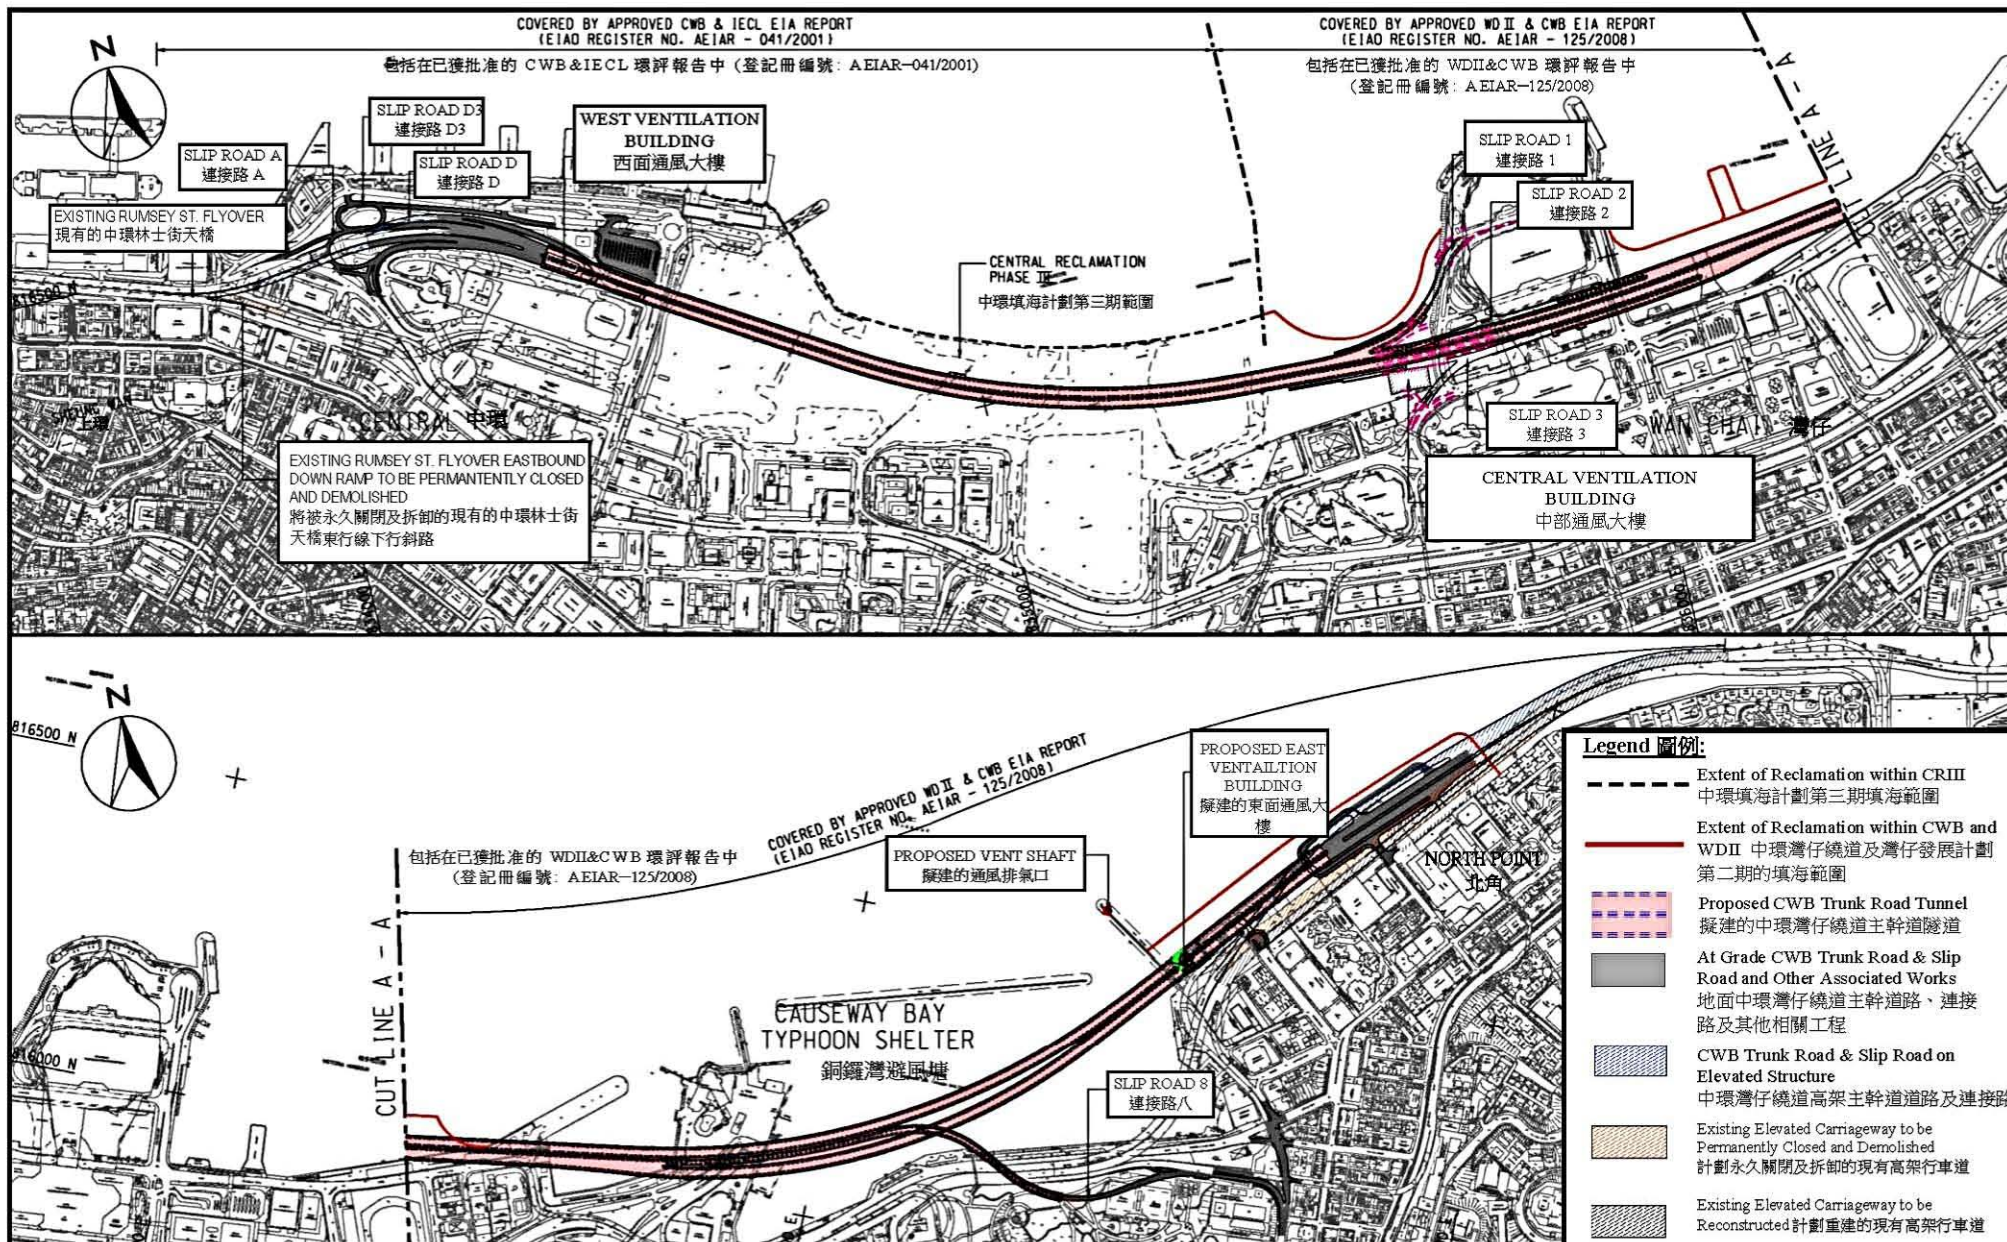Project Layout



Project Title: Central-Wanchai Bypass (CWB) Including Its Road Tunnel and Slip Roads
工程項目名稱: 中環灣仔繞道包括其行車隧道及連接路

Environmental Permit No.: EP-364/2009/E
環境許可證編號: EP-364/2009/E

Figure 1: Location of the Project
圖 1: 工程項目位置

(This figure was prepared based on Figure 1.1 of the Application for Environmental Permit (Application No.: AEP-364/2009))
(本圖是根據環境許可證的申請(申請書編號 AEP-364/2009 圖 1.1 編製))



Figure 2.2

Project Organization Chart



Project Organization Chart

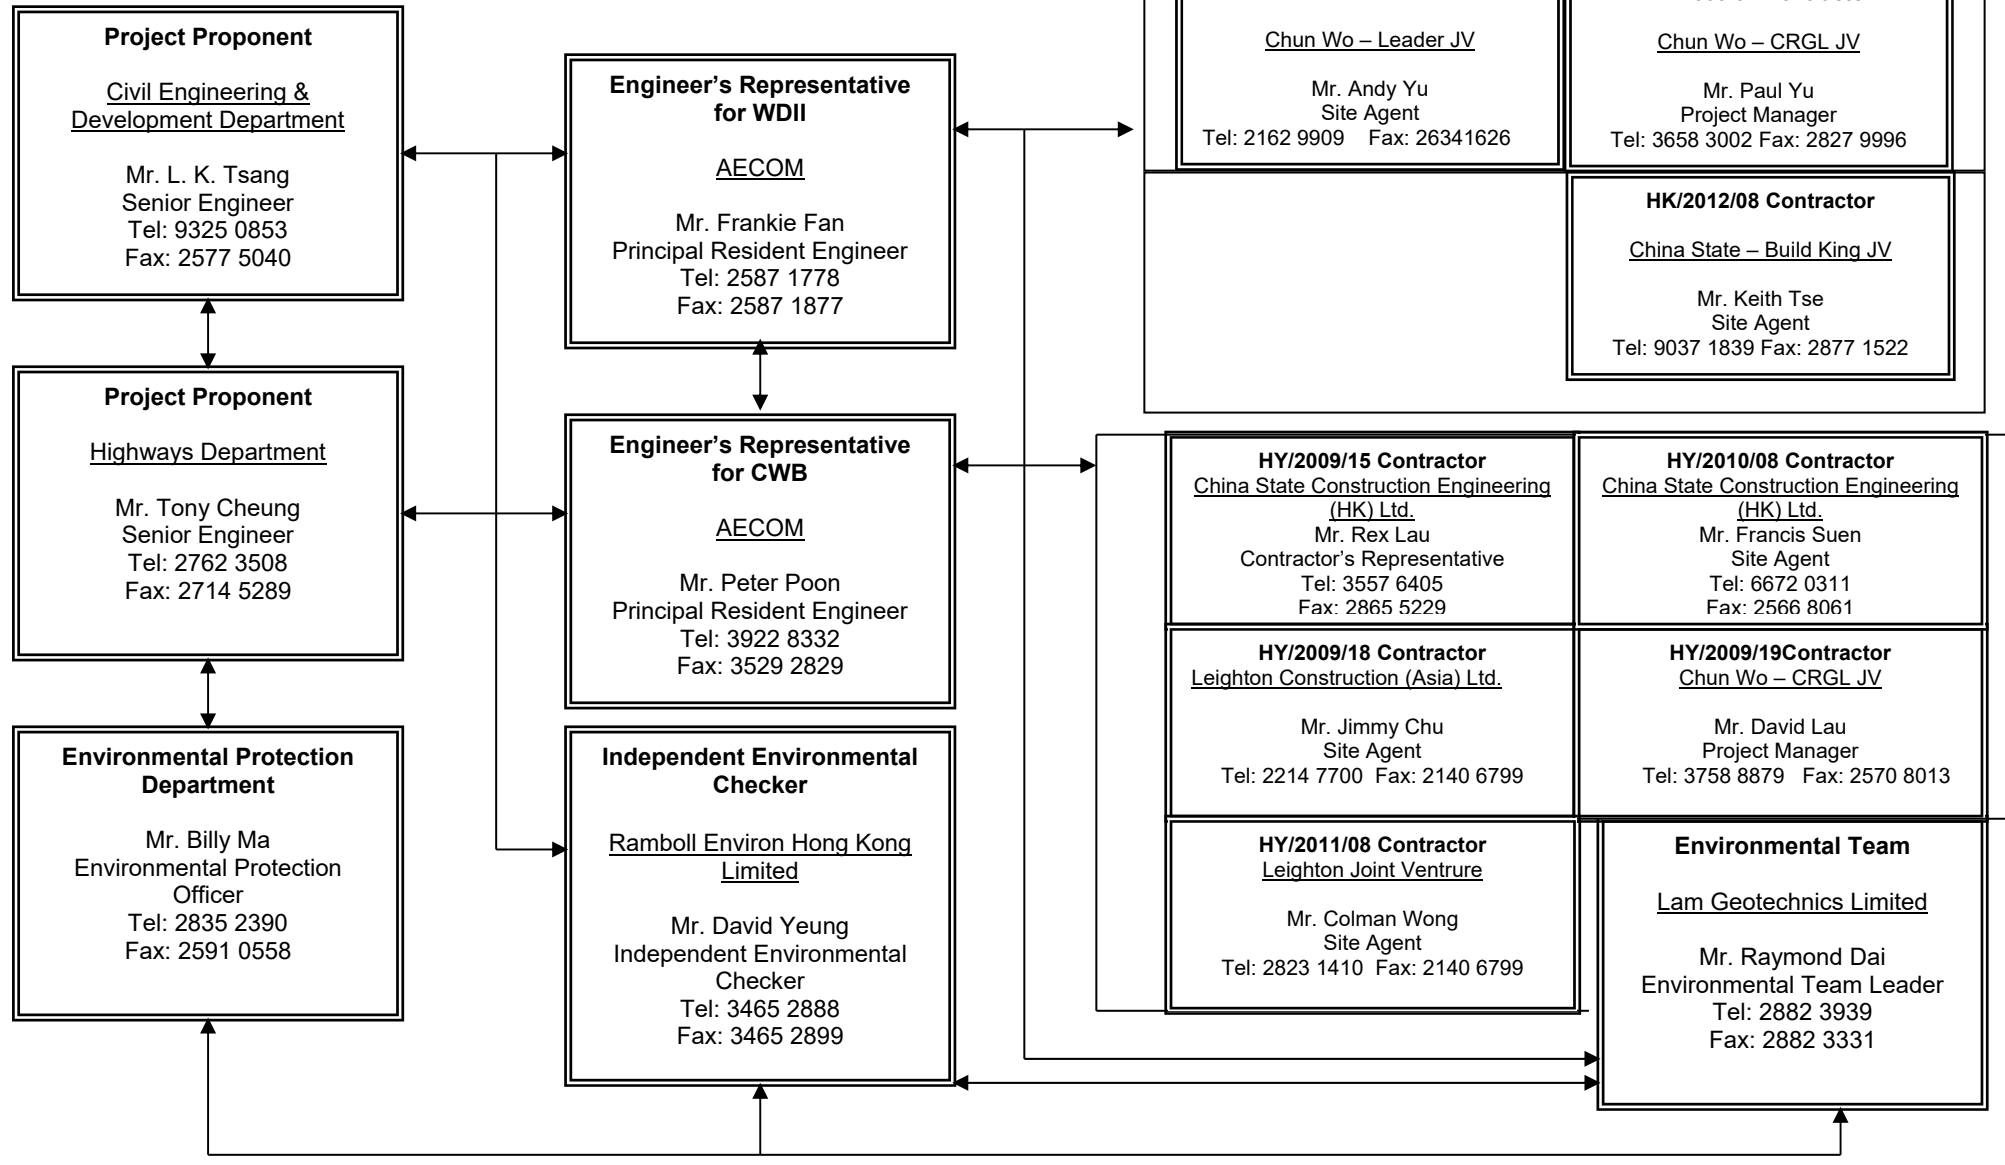


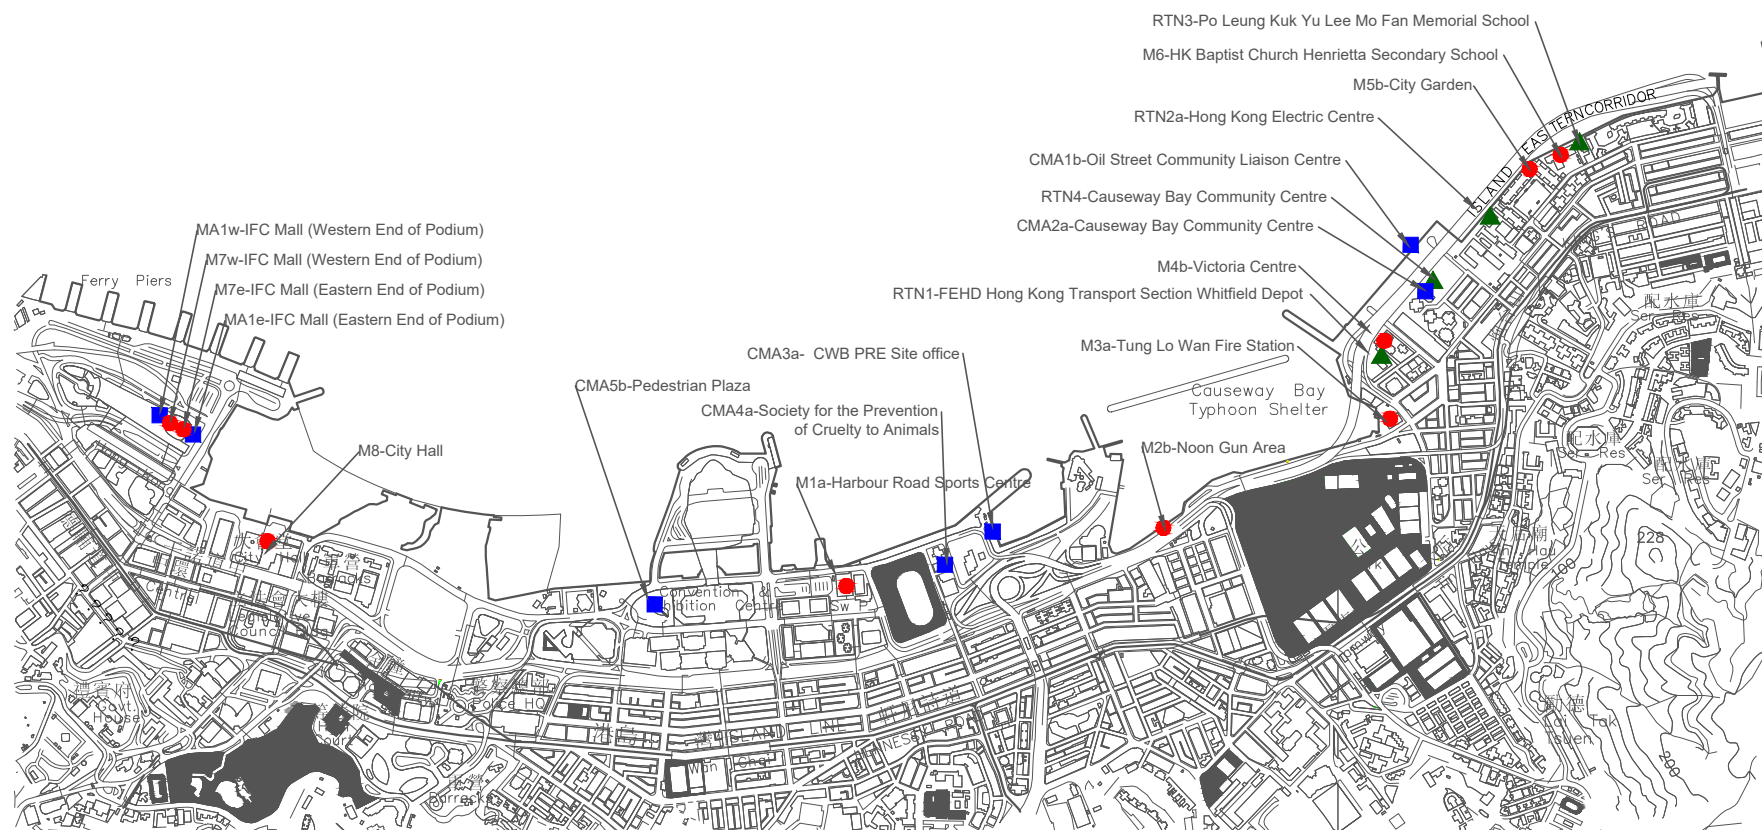


Figure 3.1

Locations of Monitoring Stations

Legend

- Noise Monitoring Station
- Air Quality Monitoring Station
- ▲ Real-time Noise Monitoring Station



LOCATIONS OF AIR QUALITY AND NOISE MONITORING STATIONS



Appendix 2.1

Environmental Mitigation Implementation Schedule

IMPLEMENTATION SCHEDULE OF THE PROPOSED MITIGATION MEASURES

Table A.1 Implementation Schedule for Air Quality Control

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
S3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor		√			EIAO-TM
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts. - Strictly limit the truck speed on site to be low 10 km per hour and water spraying to keep the haul roads in wet condition; - Watering during excavation and material handling; - Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and - Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.	Work site / during construction	Contractor		√			
Operational Phase								
S3.6.53 – S3.6.54	The design parameters of the East and Central Ventilation Buildings as set in Tables 3.10 and 3.11 of Volume 1 of the WDII & CWB EIA Report.	East and Central Ventilation Buildings / During operation of the Trunk Road	HyD			√		
S3.10.2	Air quality monitoring for the operation performance of the East Ventilation Building and associated East Vent Shaft will be conducted.	East Vent Shaft / During operation of the East Ventilation Building and associated East Vent Shaft	HyD			√		EIAO-TM

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table A.2 Implementation Schedule for Noise Control

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
S4.9.3	Good Site Practice: - Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program. - Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program. - Mobile plant, if any, shall be sited as far away from NSRs as possible. - Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum. - Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. - Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from on-site construction activities.	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
S4.8.1 – S4.8.11	Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks: - Slip road & tunnel - Construction of diaphragm wall and substructures of the tunnel approach ramp - Excavation - Construction of slabs - Backfill	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	- Demolition and construction of substructures for the IEC - Demolition works of existing piers and cross heads of the marine section of the existing IEC Use of PME grouping for the following tasks: - At-grade road construction - Substructure for IECL connection							
Operation Phase								
S4.8.12 – S4.8.23	For Existing NSRs - about 235m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC - about 230m length of noise semi-enclosure with transparent panel covering the main carriageways (eastbound and westbound) of the CWB and IEC - about 135m length of 5.5m high cantilevered noise barrier with 4.5m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC (amended under EP-364/2009/A) - about 95m length of 5.5m high cantilevered noise barrier with 1m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC - about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC - low noise road surfacing for the trunk road (except tunnel section and beneath the landscaped deck at the eastern portal area)) with speed limit of 70 km/hour	Near North Point / Before commencement of operation of road project	HyD	√	√	√	EIAO-TM	

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	For Future/Planned NSRs - about 265m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC - The openable windows of the temple, if any, should be orientated so as to avoid direct line of sight to the existing Victoria Park Road as far as practicable.	In between the Electric Centre (next to City Garden) and CDA(1) site / Before occupation of Planned NSRs in CDA and CDA(1) sites. Near Causeway Bay Fire Station / During detailed design of the re-provisioned Tin Hau Temple	HyD Project Proponent for the re-provisioned Tin Hau Temple	√ √	#			

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Only the steel frame for this section of noise semi-enclosure would be erected in advance during the construction of the westbound slip road.

Table A.4 Implementation Schedule for Waste Management

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
S6.5.14	Floating Refuse During the construction phase, the project proponent's contractor will be responsible for the collection of any refuse within their works area. Floating booms will be provided on the water surface to confine the refuse from the working barges as well as to avoid the accumulation of pollutants within temporary embayment as mentioned in Table D9.3.	Work site / During the construction period	Contractor		√			
S6.6.1	Good Site Practices Recommendations for good site practices during the construction activities include: • nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; • training of site personnel in proper waste management and chemical waste handling procedures; • provision of sufficient waste disposal points and regular collection for disposal; • appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; • regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and • a recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).	Work site / During the construction period	Contractor		√			Waste Disposal Ordinance (Cap.354)

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.6.2	<i>Waste Reduction Measures</i> Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include: • segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; • to encourage collection of aluminium cans, PET bottles and paper, separate labelled bins shall be provided to segregate these wastes from other general refuse generated by the work force; • any unused chemicals or those with remaining functional capacity shall be recycled; • use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&D material. • prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill; • proper storage and site practices to minimise the potential for damage or contamination of construction materials; and • plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	Work site / During planning and design stage, and construction stage	Contractor	√	√			

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.6.4	<i>General Refuse</i> General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material. A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.	Work site / During the construction period	Contractor		√			Public Health and Municipal Services Ordinance (Cap. 132)
S6.6.5	<i>Chemical Wastes</i> After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	Contractor		√			Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.6.6	<i>Construction and Demolition Material</i> C&D material shall be sorted on-site into inert C&D material (that is, public fill) and C&D waste. All the suitable inert C&D material shall be broken down to 250 mm in size for re use as public fill in the WDII reclamation. C&D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.	Work site / During the construction period	Contractor		√			ETWB TCW No. 33/2002, 31/2004, 19/2005

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.6.7	In order to monitor the disposal of public fill and C&D waste at public fill reception facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.	Work site / During the construction period	Contractor and Independent Environmental Checker		√			ETWB TCW No. 31/2004
S6.6.8	<i>Bentonite Slurry</i> The disposal of residual used bentonite slurry shall follow the good practice guidelines stated in ProPECC PN 1/94 “Construction Site Drainage” and listed as follows: • If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis. • If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters. • If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal.	Work site / During the construction period	Contractor		√			ProPECC PN 1/94

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table A.5 Implementation Schedule for Land Contamination

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction and Operation Phase								
S.7.1.1	As no potential contaminative land uses were identified within the Study Area, adverse land contamination impacts associated with the construction and operation of the Project is not expected. As such, environmental protection and mitigation measures are considered not necessary and will not be covered in this EM&A Manual.	--						-

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table A.7 Implementation Schedule for Landscape and Visual

WDII & CWB EIA Report Ref	Environmental Protection Measures / Mitigation Measures		Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
					Des	C	O	Dec	
Construction Phase									
Table 10.5	CM1	Topsoil, where identified, shall be stripped and stored for re-use i n t he c onstruction of the soft l andscape works, where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM2	Existing t rees t o be retained on si te shall be car efully protected during construction.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM3	Trees unavoidably affected b y t he works s hall b e transplanted where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM4	Compensatory tree pl anting sha ll b e provi ded to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM5	Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6	Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Operation Phase									
Table 10.6, Figure 10.5.1-10.5.5	OM1	Aesthetic design of b uildings and road-related structures, including v iaducts, ve nt buildings, subw ays, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	HyD	√	√	√	ETW	B TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM3	Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	HyD	√	√	√	ETW	B TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM5	Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	HyD	√	√	√	ETW	B TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM6	Aesthetic design of roadside amenity areas.	Work site / During Design Stage and Operation Phases	HyD	√	√	√	ETW	B TCW 2/2004

*Des - Design, C - Construction, O – Operation, and Dec - Decommissioning



Appendix 3.1

Action and Limit Level

Action and Limit Level

Action and Limit Level for Noise Monitoring

Time Period	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A)/ 70 dB(A)/ 65 dB(A) ^{Note 1}

Note 1:

- 70dB(A) and 65 dB(A) for schools during normal teaching periods and school examination periods, respectively.
- If works are to be carried out during the restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

Action and Limit Level for Air Monitoring

Monitoring Location	1-hour TSP Level in $\mu\text{g}/\text{m}^3$		24-hour TSP Level in $\mu\text{g}/\text{m}^3$	
	Action Level	Limit Level	Action Level	Limit Level
CMA1b	320.1	500	176.7	260
CMA2a	323.4	500	169.5	260
CMA3a	311.3	500	171.0	260
CMA4a	312.5	500	171.2	260
CMA5b	332.0	500	181.0	260
MA1e	325.1	500	173.4	260
MA1w	325.1	500	173.4	260



Appendix 4.1

Noise Monitoring Results and Graphical Presentations



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M1a - Harbour Road Sports Centre

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
27/2/2017	10:10	Fine	76.8	80.0	73.0	72	75	75
7/3/2017	10:40	Fine	77.1	78.5	72.5	72	75	75
13/3/2017	10:15	Cloudy	76.4	78.5	72.0	72	74	75
20/3/2017	11:00	Fine	76.5	77.9	73.5	72	74	75

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq	Leq	Leq	
			Unit: dB(A), (30-min)						
27/2/2017	10:53	Fine	67.0	69.0	65.5	68	67	75	
7/3/2017	11:30	Fine	71.0	73.5	67.5	68	68	75	
13/3/2017	11:15	Cloudy	68.8	70.0	67.0	68	63	75	
21/3/2017	14:00	Fine	68.2	69.5	65.0	68	59	75	

Location: M3a - Tung Lo Wan Fire Station

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
28/2/2017	10:22	Cloudy	67.5	69.5	64.0	69	68	75
7/3/2017	13:30	Fine	67.5	68.2	64.5	69	68	75
14/3/2017	13:45	Cloudy	67.1	68.5	65.0	69	67	75
21/3/2017	14:40	Fine	67.0	69.0	62.4	69	67	75

Location: M4b - Victoria Centre

Date	Time	Weather	Measurement Noise Level			Baseline Noise Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30min)								
28/2/2017	11:00	Cloudy	64.4	65.5	61.0	67	64	75
7/3/2017	14:12	Fine	65.5	67.0	63.0	67	66	75
14/3/2017	14:20	Cloudy	65.6	67.0	63.5	67	66	75
21/3/2017	15:18	Fine	64.5	65.5	62.5	67	65	75

Location: M5b - City Garden

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq	Leq	Leq	
			Unit: dB(A), (30min)						
28/2/2017	13:00	Cloudy	67.6	69.5	64.5	68	68	75	
7/3/2017	14:55	Fine	67.9	69.5	65.0	68	68	75	
14/3/2017	15:30	Cloudy	76.0	77.0	71.5	68	75	75	
21/3/2017	16:00	Fine	71.3	72.0	66.5	68	69	75	

Location: M6 - HK Baptist Church Henrietta Secondary School

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq	Leq	Leq	
			Unit: dB(A), (30-min)						
28/2/2017	13:40	Cloudy	69.4	72.0	63.5	71	69	70	
7/3/2017	15:33	Fine	71.9	73.0	70.0	71	66	70	
14/3/2017	16:06	Cloudy	71.2	72.5	68.0	71	62	70	
21/3/2017	16:35	Fine	71.0	72.5	68.5	71	59	70	



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M7e - International Finance Centre (Eastern End of Podium) (Reference Station)

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq	Leq	Leq	
			Unit: dB(A), (30-min)						
28/2/2017	08:05	Cloudy	64.5	65.5	62.0	67	65	N/A	
7/3/2017	08:00	Fine	66.0	67.5	64.5	67	66	N/A	
14/3/2017	09:45	Cloudy	66.9	68.5	64.0	67	50	N/A	
21/3/2017	08:30	Fine	65.5	66.5	63.0	67	66	N/A	

Location: M7w - International Finance Centre (Western End of Podium)

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
28/2/2017	08:45	Cloudy	62.0	65.5	60.0	69	62	75
7/3/2017	08:45	Fine	63.5	64.5	62.5	69	64	75
14/3/2017	10:30	Cloudy	65.2	66.5	62.5	69	65	75
21/3/2017	09:35	Fine	63.5	64.5	61.0	69	64	75

Location: M8 - City Hall

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
28/2/2017	09:20	Cloudy	60.0	62.5	58.5	64	60	70
7/3/2017	09:30	Fine	58.5	60.5	57.0	64	59	70
14/3/2017	11:28	Cloudy	62.5	64.5	57.5	64	63	70
21/3/2017	10:35	Fine	62.0	63.0	58.5	64	62	70



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M1a - Harbour Road Sports Centre

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
28/3/2017	09:50	Fine	75.1	76.5	71.0	72	72	75
3/4/2017	14:42	Fine	74.5	75.5	70.9	72	71	75
11/4/2017	13:40	Cloudy	74.5	76.0	71.0	72	71	75
18/4/2017	10:00	Fine	73.6	75.5	70.0	72	68	75
24/4/2017	13:46	Cloudy	76.4	78.0	74.0	72	74	75

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
28/3/2017	16:40	Fine	72.2	75.0	67.2	68	70	75
3/4/2017	13:46	Fine	74.9	78.5	67.5	68	74	75
11/4/2017	14:30	Cloudy	70.2	72.5	67.0	68	67	75
18/4/2017	10:45	Fine	71.8	74.5	67.0	68	70	75
24/4/2017	14:30	Fine	70.1	72.0	67.0	68	67	75

Location: M3a - Tung Lo Wan Fire Station

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
28/3/2017	13:10	Fine	66.4	67.5	64.0	69	66	75
3/4/2017	13:05	Fine	66.5	67.5	64.5	69	67	75
11/4/2017	15:15	Cloudy	65.4	66.5	63.0	69	65	75
18/4/2017	11:30	Fine	66.9	68.0	64.5	69	67	75
24/4/2017	16:04	Cloudy	64.7	66.0	62.0	69	65	75

Location: M4b - Victoria Centre

Date	Time	Weather	Measurement Noise Level			Baseline Noise Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq	Leq	Leq	
			Unit: dB(A), (30min)						Leq
28/3/2017	13:55	Fine	64.2	65.5	62.0	67	64	75	
3/4/2017	11:30	Fine	69.7	71.5	61.5	67	66	75	
11/4/2017	15:50	Cloudy	66.4	67.5	63.5	67	66	75	
18/4/2017	13:00	Fine	65.9	67.5	63.5	67	66	75	
24/4/2017	15:15	Cloudy	71.7	74.0	65.0	67	70	75	

Location: M5b - City Garden

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30min)					
28/3/2017	14:45	Fine	75.8	77.5	72.5	68	75	75
3/4/2017	10:58	Fine	69.4	70.0	66.0	68	64	75
10/4/2017	10:41	Cloudy	71.0	72.5	68.0	68	68	75
18/4/2017	13:50	Fine	78.4	80.0	74.0	68	78	75
28/4/2017	10:49	Cloudy	69.0	70.0	67.0	68	62	75

Location: M6 - HK Baptist Church Henrietta Secondary School

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
28/3/2017	15:25	Fine	71.4	72.5	68.0	71	63	70
3/4/2017	09:45	Fine	70.1	71.0	67.0	71	70	65
10/4/2017	09:26	Cloudy	68.0	69.0	66.5	71	68	65
18/4/2017	15:00	Fine	70.0	76.0	67.0	71	70	70
26/4/2017	14:30	Cloudy	67.8	69.0	66.0	71	68	65



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M7e - International Finance Centre (Eastern End of Podium) (Reference Station)

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
27/3/2017	08:30	Fine	65.5	66.0	62.5	67	66	N/A
5/4/2017	14:29	Fine	66.1	67.5	62.5	67	66	N/A
11/4/2017	17:00	Cloudy	67.3	66.0	62.0	67	58	N/A
18/4/2017	16:30	Fine	75.6	78.5	64.5	67	75	N/A
24/4/2017	10:20	Cloudy	60.2	62.0	60.0	67	60	N/A

Location: M7w - International Finance Centre (Western End of Podium)

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
27/3/2017	09:30	Fine	63.5	65.0	60.5	69	64	75
5/4/2017	13:53	Fine	65.9	67.5	63.0	69	66	75
11/4/2017	16:25	Cloudy	64.3	65.5	61.5	69	64	75
18/4/2017	15:58	Fine	64.7	66.0	62.0	69	65	75
24/4/2017	09:48	Cloudy	68.6	71.5	65.5	69	69	75

Location: M8 - City Hall

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
27/3/2017	10:35	Fine	59.5	60.5	57.0	64	60	70
5/4/2017	15:15	Fine	64.7	67.5	63.1	64	56	70
11/4/2017	17:35	Cloudy	65.6	66.4	61.9	64	60	70
18/4/2017	17:08	Fine	65.8	68.3	60.9	64	61	70
24/4/2017	11:06	Cloudy	68.1	72.5	60.5	64	66	70



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M1a - Harbour Road Sports Centre

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
2/5/2017	13:30	Fine	75.5	77.0	73.0	72	73	75
8/5/2017	14:48	Fine	75.5	76.1	70.5	72	73	75
16/5/2017	13:48	Cloudy	78.0	80.5	73.3	72	77	75
25/5/2017	10:45	Fine	78.2	79.5	75.7	72	77	75

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
2/5/2017	14:11	Fine	69.2	71.0	66.5	68	64	75
8/5/2017	15:37	Fine	70.5	72.0	65.5	68	67	75
18/5/2017	14:00	Cloudy	68.5	70.5	65.5	68	61	75
26/5/2017	14:00	Fine	69.3	70.9	66.9	68	64	75

Location: M3a - Tung Lo Wan Fire Station

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
2/5/2017	14:55	Fine	66.1	67.0	64.5	69	66	75
9/5/2017	10:00	Fine	66.4	67.5	63.5	69	66	75
15/5/2017	15:00	Fine	71.4	73.0	62.5	69	68	75
25/5/2017	13:20	Fine	66.5	67.5	65.3	69	67	75

Location: M4b - Victoria Centre

Date	Time	Weather	Measurement Noise Level			Baseline Noise Level	Construction Noise Level		Limit Level
			Leq	L10	L90	Leq	Leq	Leq	
			Unit: dB(A), (30min)						
4/5/2017	15:27	Cloudy	64.8	66.0	62.5	67	65	75	
9/5/2017	10:50	Fine	66.1	67.0	63.5	67	66	75	
16/5/2017	15:45	Fine	65.3	66.5	63.0	67	65	75	
25/5/2017	14:05	Fine	71.6	75.1	66.7	67	70	75	

Location: M5b - City Garden

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30min)					
4/5/2017	16:10	Cloudy	70.5	74.0	67.5	68	67	75
10/5/2017	10:05	Fine	72.8	74.5	67.5	68	71	75
18/5/2017	15:40	Fine	73.1	74.0	69.0	68	71	75
25/5/2017	14:55	Fine	74.9	76.1	71.0	68	74	75

Location: M6 - HK Baptist Church Henrietta Secondary School

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
4/5/2017	16:55	Cloudy	66.8	67.5	65.0	71	67	70
10/5/2017	10:45	Fine	68.4	69.5	65.3	71	68	70
18/5/2017	15:00	Fine	69.8	70.5	66.5	71	70	70
25/5/2017	15:30	Fine	64.4	65.8	62.3	71	64	70



Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

Location: M7e - International Finance Centre (Eastern End of Podium) (Reference Station)


Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
2/5/2017	10:55	Cloudy	63.9	66.0	61.0	67	64	N/A
8/5/2017	10:53	Fine	66.8	68.5	62.0	67	67	N/A
17/5/2017	15:48	Fine	68.4	69.5	65.0	67	63	N/A
25/5/2017	09:50	Fine	71.1	74.0	68.0	67	69	N/A


Location: M7w - International Finance Centre (Western End of Podium)

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
2/5/2017	10:20	Fine	66.0	67.5	63.5	69	66	75
8/5/2017	10:20	Fine	63.9	65.5	61.5	69	64	75
17/5/2017	15:15	Fine	67.4	69.0	62.0	69	67	75
25/5/2017	09:15	Fine	67.2	69.0	64.6	69	67	75

Location: M8 - City Hall


Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
			Unit: dB(A), (30-min)					
2/5/2017	11:30	Fine	64.5	66.5	61.5	64	55	70
8/5/2017	11:30	Fine	61.0	63.8	60.0	64	61	70
17/5/2017	16:27	Fine	66.2	67.5	63.0	64	62	70
25/5/2017	08:15	Fine	61.1	63.0	56.8	64	61	70

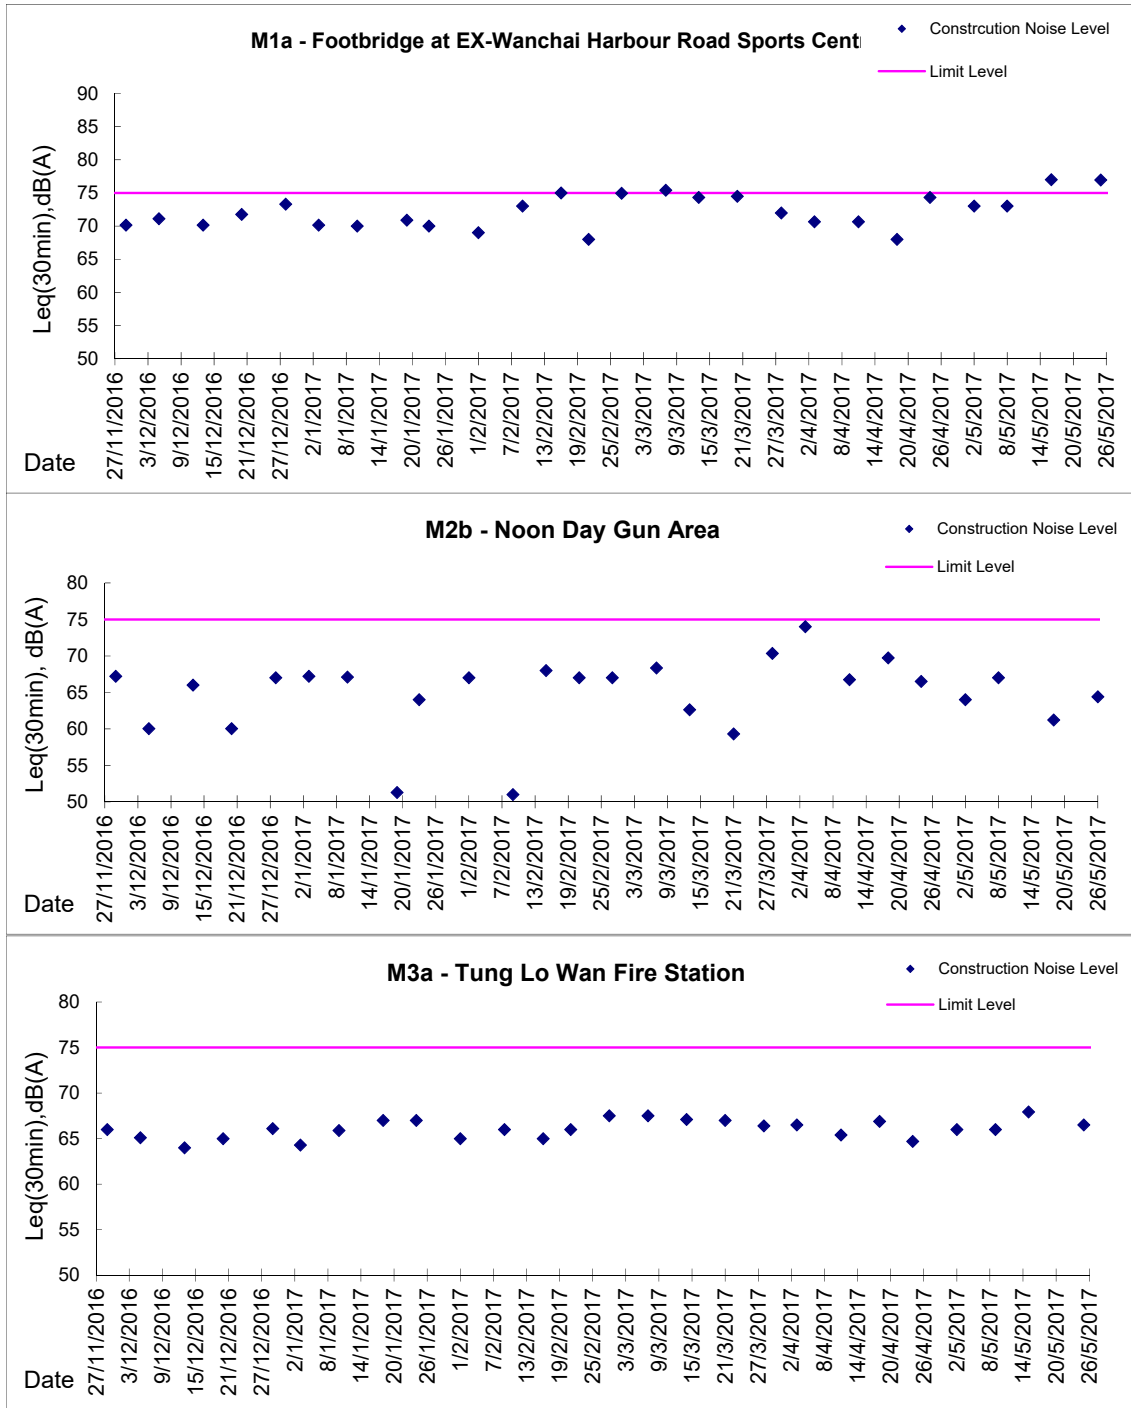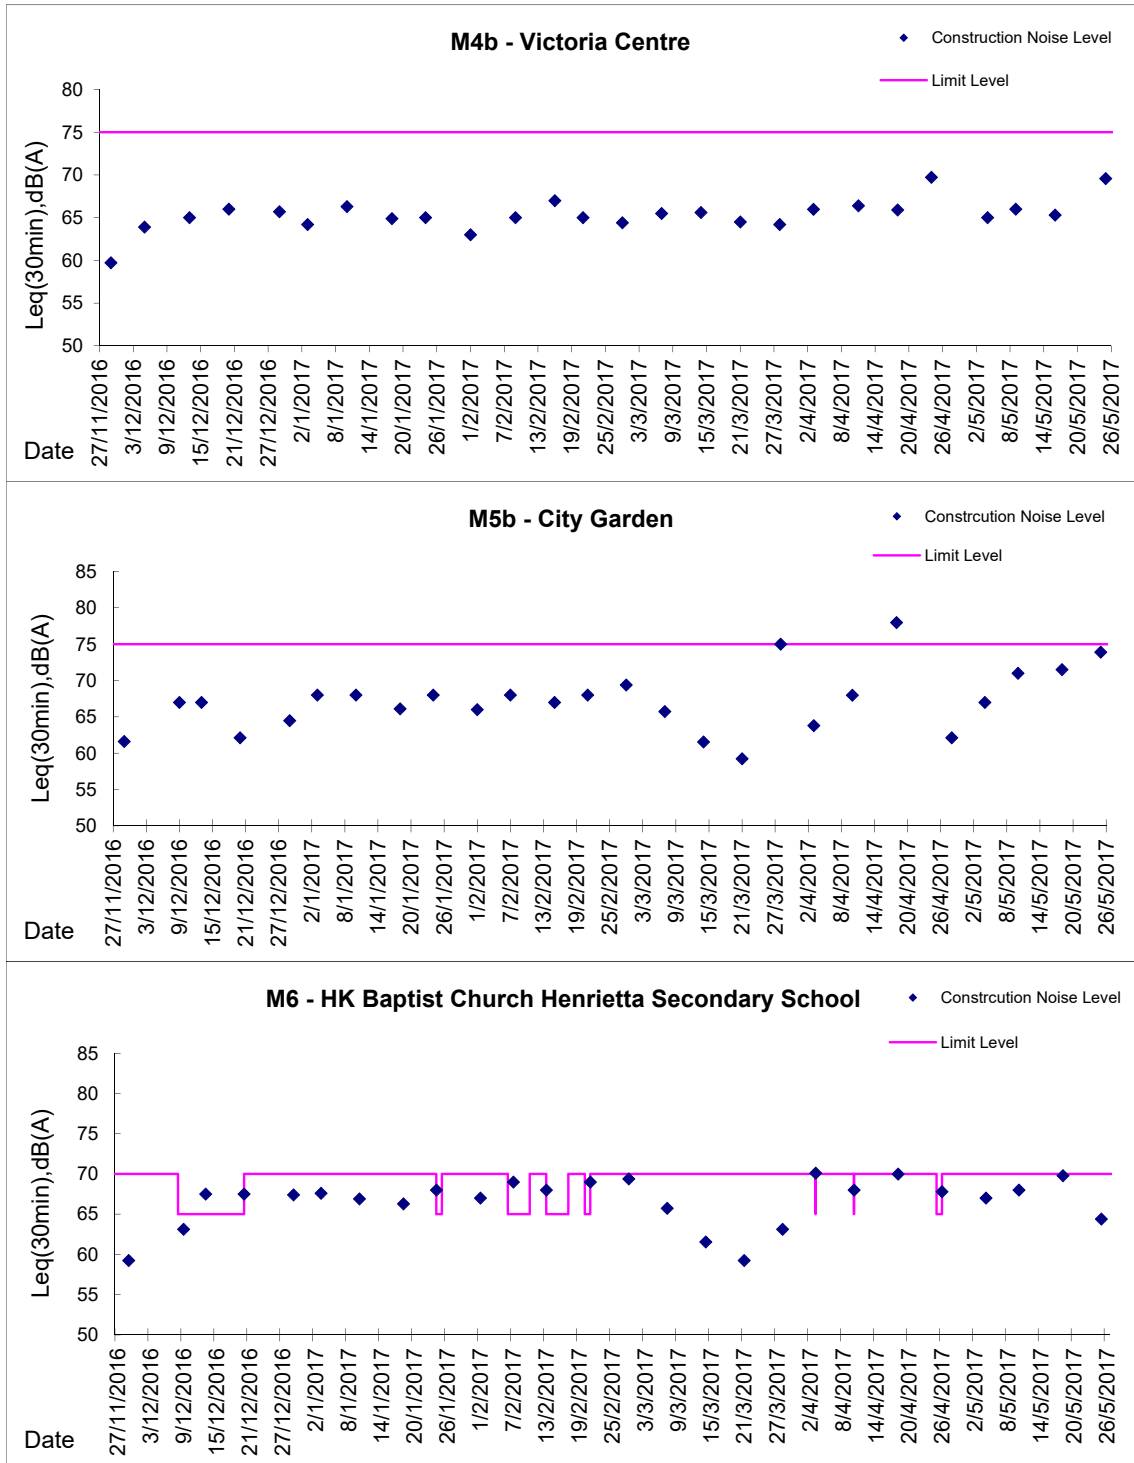Graphic Presentation of Noise Monitoring Result
Day Time (0700 - 1900hrs on normal weekdays)


Graphic Presentation of Noise Monitoring Result
Day Time (0700 - 1900hrs on normal weekdays)


Graphic Presentation of Noise Monitoring Result

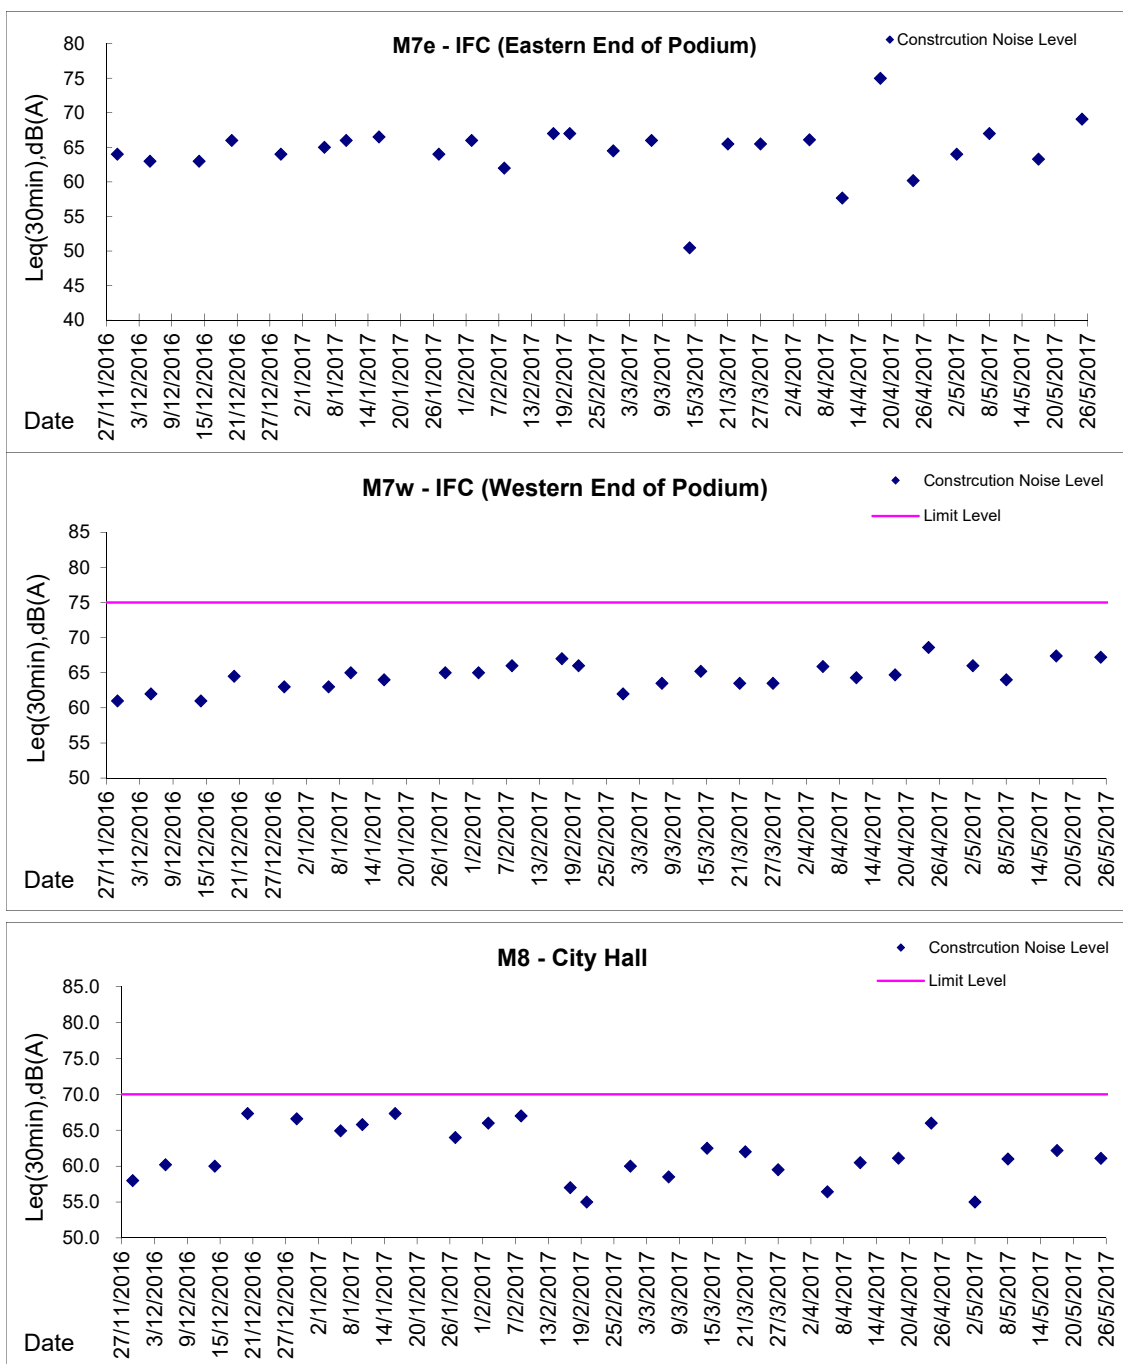Day Time (0700 - 1900hrs on normal weekdays)



* Remark: M7e - IFC (Eastern End of Podium) is a reference monitoring station



Appendix 4.2

Real Time Noise Monitoring Results and Graphical Presentations

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
Normal Day 07:00-19:00		3/3/2017 12:31	66	9/3/2017 7:01	65	14/3/2017 13:31	67	20/3/2017 8:01	67	24/3/2017 14:31	65
		3/3/2017 13:01	66	9/3/2017 7:31	66	14/3/2017 14:01	67	20/3/2017 8:31	65	24/3/2017 15:01	65
27/2/2017 7:01	64	3/3/2017 13:31	66	9/3/2017 8:01	66	14/3/2017 14:31	67	20/3/2017 9:01	65	24/3/2017 15:31	65
27/2/2017 7:31	66	3/3/2017 14:01	66	9/3/2017 8:31	66	14/3/2017 15:01	66	20/3/2017 9:31	66	24/3/2017 16:01	65
27/2/2017 8:01	66	3/3/2017 14:31	66	9/3/2017 9:01	65	14/3/2017 15:31	66	20/3/2017 10:01	66	24/3/2017 16:31	65
27/2/2017 8:31	65	3/3/2017 15:01	66	9/3/2017 9:31	66	14/3/2017 16:01	66	20/3/2017 10:31	67	24/3/2017 17:01	66
27/2/2017 9:01	65	3/3/2017 15:31	66	9/3/2017 10:01	67	14/3/2017 16:31	66	20/3/2017 11:01	66	24/3/2017 17:31	66
27/2/2017 9:31	66	3/3/2017 16:01	66	9/3/2017 10:31	67	14/3/2017 17:01	66	20/3/2017 11:31	66	24/3/2017 18:01	66
27/2/2017 10:01	66	3/3/2017 16:31	67	9/3/2017 11:01	66	14/3/2017 17:31	66	20/3/2017 12:01	66	24/3/2017 18:31	65
27/2/2017 10:31	66	3/3/2017 17:01	67	9/3/2017 11:31	66	14/3/2017 18:01	66	20/3/2017 12:31	66	25/3/2017 7:01	63
27/2/2017 11:01	66	3/3/2017 17:31	67	9/3/2017 12:01	65	14/3/2017 18:31	65	20/3/2017 13:01	67	25/3/2017 7:31	65
27/2/2017 11:31	65	3/3/2017 18:01	65	9/3/2017 12:31	66	15/3/2017 7:01	65	20/3/2017 13:31	66	25/3/2017 8:01	66
27/2/2017 12:01	65	3/3/2017 18:31	65	9/3/2017 13:01	67	15/3/2017 7:31	66	20/3/2017 14:01	66	25/3/2017 8:31	66
27/2/2017 12:31	66	4/3/2017 7:01	63	9/3/2017 13:31	67	15/3/2017 8:01	66	20/3/2017 14:31	66	25/3/2017 9:01	66
27/2/2017 13:01	66	4/3/2017 7:31	65	9/3/2017 14:01	66	15/3/2017 8:31	65	20/3/2017 15:01	66	25/3/2017 9:31	66
27/2/2017 13:31	66	4/3/2017 8:01	66	9/3/2017 14:31	66	15/3/2017 9:01	66	20/3/2017 15:31	66	25/3/2017 10:01	66
27/2/2017 14:01	66	4/3/2017 8:31	66	9/3/2017 15:01	66	15/3/2017 9:31	67	20/3/2017 16:01	66	25/3/2017 10:31	66
27/2/2017 14:31	66	4/3/2017 9:01	66	9/3/2017 15:31	66	15/3/2017 10:01	66	20/3/2017 16:31	66	25/3/2017 11:01	66
27/2/2017 15:01	66	4/3/2017 9:31	66	9/3/2017 16:01	66	15/3/2017 10:31	67	20/3/2017 17:01	66	25/3/2017 11:31	66
27/2/2017 15:31	66	4/3/2017 10:01	67	9/3/2017 16:31	66	15/3/2017 11:01	67	20/3/2017 17:31	66	25/3/2017 12:01	65
27/2/2017 16:01	66	4/3/2017 10:31	67	9/3/2017 17:01	66	15/3/2017 11:31	66	20/3/2017 18:01	65	25/3/2017 12:31	66
27/2/2017 16:31	66	4/3/2017 11:01	66	9/3/2017 17:31	65	15/3/2017 12:01	66	20/3/2017 18:31	65	25/3/2017 13:01	67
27/2/2017 17:01	66	4/3/2017 11:31	65	9/3/2017 18:01	65	15/3/2017 12:31	66	21/3/2017 7:01	64	25/3/2017 13:31	66
27/2/2017 17:31	66	4/3/2017 12:01	65	9/3/2017 18:31	66	15/3/2017 13:01	67	21/3/2017 7:31	66	25/3/2017 14:01	66
27/2/2017 18:01	67	4/3/2017 12:31	65	10/3/2017 7:01	65	15/3/2017 13:31	67	21/3/2017 8:01	66	25/3/2017 14:31	65
27/2/2017 18:31	66	4/3/2017 13:01	67	10/3/2017 7:31	65	15/3/2017 14:01	67	21/3/2017 8:31	65	25/3/2017 15:01	65
28/2/2017 7:01	64	4/3/2017 13:31	67	10/3/2017 8:01	64	15/3/2017 14:31	66	21/3/2017 9:01	65	25/3/2017 15:31	65
28/2/2017 7:31	65	4/3/2017 14:01	67	10/3/2017 8:31	65	15/3/2017 15:01	66	21/3/2017 9:31	66	25/3/2017 16:01	65
28/2/2017 8:01	66	4/3/2017 14:31	65	10/3/2017 9:01	65	15/3/2017 15:31	66	21/3/2017 10:01	66	25/3/2017 16:31	66
28/2/2017 8:31	66	4/3/2017 15:01	65	10/3/2017 9:31	66	15/3/2017 16:01	66	21/3/2017 10:31	66	25/3/2017 17:01	67
28/2/2017 9:01	65	4/3/2017 15:31	65	10/3/2017 10:01	66	15/3/2017 16:31	66	21/3/2017 11:01	66	25/3/2017 17:31	66
28/2/2017 9:31	65	4/3/2017 16:01	65	10/3/2017 10:31	66	15/3/2017 17:01	66	21/3/2017 11:31	65	25/3/2017 18:01	65
28/2/2017 10:01	67	4/3/2017 16:31	65	10/3/2017 11:01	66	15/3/2017 17:31	66	21/3/2017 12:01	65	25/3/2017 18:31	65
28/2/2017 10:31	67	4/3/2017 17:01	66	10/3/2017 11:31	66	15/3/2017 18:01	66	21/3/2017 12:31	66		
28/2/2017 11:01	66	4/3/2017 17:31	66	10/3/2017 12:01	65	15/3/2017 18:31	66	21/3/2017 13:01	66	Normal Day 19:00-23:00	
28/2/2017 11:31	66	4/3/2017 18:01	65	10/3/2017 12:31	65	16/3/2017 7:01	64	21/3/2017 13:31	66	Sunday & Holiday	
28/2/2017 12:01	66	4/3/2017 18:31	65	10/3/2017 13:01	66	16/3/2017 7:31	66	21/3/2017 14:01	66	07:00-23:00	
28/2/2017 12:31	66	6/3/2017 7:01	64	10/3/2017 13:31	66	16/3/2017 8:01	67	21/3/2017 14:31	66	27/2/2017 19:01	67
28/2/2017 13:01	66	6/3/2017 7:31	64	10/3/2017 14:01	66	16/3/2017 8:31	66	21/3/2017 15:01	66	27/2/2017 19:06	66
28/2/2017 13:31	66	6/3/2017 8:01	64	10/3/2017 14:31	66	16/3/2017 9:01	66	21/3/2017 15:31	66	27/2/2017 19:11	66
28/2/2017 14:01	66	6/3/2017 8:31	64	10/3/2017 15:01	66	16/3/2017 9:31	66	21/3/2017 16:01	66	27/2/2017 19:16	66
28/2/2017 14:31	66	6/3/2017 9:01	65	10/3/2017 15:31	66	16/3/2017 10:01	66	21/3/2017 16:31	66	27/2/2017 19:21	66
28/2/2017 15:01	65	6/3/2017 9:31	66	10/3/2017 16:01	66	16/3/2017 10:31	66	21/3/2017 17:01	66	27/2/2017 19:26	66
28/2/2017 15:31	65	6/3/2017 10:01	66	10/3/2017 16:31	66	16/3/2017 11:01	66	21/3/2017 17:31	66	27/2/2017 19:31	65
28/2/2017 16:01	66	6/3/2017 10:31	66	10/3/2017 17:01	66	16/3/2017 11:31	66	21/3/2017 18:01	66	27/2/2017 19:36	65
28/2/2017 16:31	66	6/3/2017 11:01	66	10/3/2017 17:31	66	16/3/2017 12:01	66	21/3/2017 18:31	65	27/2/2017 19:41	64
28/2/2017 17:01	65	6/3/2017 11:31	66	10/3/2017 18:01	65	16/3/2017 12:31	66	22/3/2017 7:01	64	27/2/2017 19:46	65
28/2/2017 17:31	65	6/3/2017 12:01	65	10/3/2017 18:31	65	16/3/2017 13:01	67	22/3/2017 7:31	65	27/2/2017 19:51	66
28/2/2017 18:01	65	6/3/2017 12:31	65	11/3/2017 7:01	62	16/3/2017 13:31	66	22/3/2017 8:01	65	27/2/2017 19:56	64
28/2/2017 18:31	66	6/3/2017 13:01	66	11/3/2017 7:31	65	16/3/2017 14:01	66	22/3/2017 8:31	65	27/2/2017 20:01	64
1/3/2017 7:01	64	6/3/2017 13:31	66	11/3/2017 8:01	66	16/3/2017 14:31	66	22/3/2017 9:01	65	27/2/2017 20:06	64
1/3/2017 7:31	65	6/3/2017 14:01	66	11/3/2017 8:31	66	16/3/2017 15:01	66	22/3/2017 9:31	65	27/2/2017 20:11	63
1/3/2017 8:01	66	6/3/2017 14:31	65	11/3/2017 9:01	66	16/3/2017 15:31	66	22/3/2017 10:01	65	27/2/2017 20:16	65
1/3/2017 8:31	66	6/3/2017 15:01	66	11/3/2017 9:31	66	16/3/2017 16:01	66	22/3/2017 10:31	65	27/2/2017 20:21	64
1/3/2017 9:01	65	6/3/2017 15:31	66	11/3/2017 10:01	66	16/3/2017 16:31	66	22/3/2017 11:01	65	27/2/2017 20:26	65
1/3/2017 9:31	65	6/3/2017 16:01	66	11/3/2017 10:31	66	16/3/2017 17:01	65	22/3/2017 11:31	65	27/2/2017 20:31	64
1/3/2017 10:01	66	6/3/2017 16:31	65	11/3/2017 11:01	66	16/3/2017 17:31	66	22/3/2017 12:01	65	27/2/2017 20:36	64
1/3/2017 10:31	66	6/3/2017 17:01	66	11/3/2017 11:31	66	16/3/2017 18:01	66	22/3/2017 12:31	65	27/2/2017 20:41	63
1/3/2017 11:01	66	6/3/2017 17:31	66	11/3/2017 12:01	65	16/3/2017 18:31	66	22/3/2017 13:01	66	27/2/2017 20:46	64
1/3/2017 11:31	66	6/3/2017 18:01	66	11/3/2017 12:31	66	17/3/2017 7:01	64	22/3/2017 13:31	67	27/2/2017 20:51	64
1/3/2017 12:01	66	6/3/2017 18:31	66	11/3/2017 13:01	66	17/3/2017 7:31	65	22/3/2017 14:01	67	27/2/2017 20:56	64
1/3/2017 12:31	66	7/3/2017 7:01	64	11/3/2017 13:31	66	17/3/2017 8:01	65	22/3/2017 14:31	66	27/2/2017 21:01	63
1/3/2017 13:01	66	7/3/2017 7:31	66	11/3/2017 14:01	67	17/3/2017 8:31	65	22/3/2017 15:01	65	27/2/2017 21:06	64
1/3/2017 13:31	67	7/3/2017 8:01	65	11/3/2017 14:31	67	17/3/2017 9:01	66	22/3/2017 15:31	66	27/2/2017 21:11	63
1/3/2017 14:01	66	7/3/2017 8:31	65	11/3/2017 15:01	66	17/3/2017 9:31	67	22/3/2017 16:01	66	27/2/2017 21:16	63
1/3/2017 14:31	66	7/3/2017 9:01	66	11/3/2017 15:31	65	17/3/2017 10:01	66	22/3/2017 16:31	67	27/2/2017 21:21	63
1/3/2017 15:01	66	7/3/2017 9:31	66	11/3/2017 16:01	65	17/3/2017 10:31	66	22/3/2017 17:01	67	27/2/2017 21:26	63
1/3/2017 15:31	66	7/3/2017 10:01	66	11/3/2017 16:31	66	17/3/2017 11:01	66	22/3/2017 17:31	67	27/2/2017 21:31	63
1/3/2017 16:01	67	7/3/2017 10:31	66	11/3/2017 17:01	66	17/3/2017 11:31	66	22/3/2017 18:01	66	27/2/2017 21:36	63
1/3/2017 16:31	66	7/3/2017 11:01	66	11/3/2017 17:31	66	17/3/2017 12:01	66	22/3/2017 18:31	66	27/2/2017 21:41	63
1/3/2017 17:01	66	7/3/2017 11:31	66	11/3/2017 18:01	65	17/3/2017 12:31	66	23/3/2017 7:01	64	27/2/2017 21:46	64
1/3/2017 17:31	65	7/3/2017 12:01	65	11/3/2017 18:31	65	17/3/2017 13:01	66	23/3/2017 7:31	66	27/2/2017 21:51	63
1/3/2017 18:01	65	7/3/2017 12:31	66	13/3/2017 7:01	64	17/3/2017 13:31	66	23/3/2017 8:01	66	27/2/2017 21:56	63
1/3/2017 18:31	66	7/3/2017 13:01	66	13/3/2017 7:31	66	17/3/2017 14:01	66	23/3/2017 8:31	65	27/2/2017 22:01	63
2/3/2017 7:01	6										

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
28/2/2017 20:56	64	2/3/2017 22:01	63	5/3/2017 7:06	66	5/3/2017 16:11	64	6/3/2017 21:16	63	8/3/2017 22:21	64
28/2/2017 21:01	65	2/3/2017 22:06	62	5/3/2017 7:11	63	5/3/2017 16:16	65	6/3/2017 21:21	63	8/3/2017 22:26	65
28/2/2017 21:06	63	2/3/2017 22:11	63	5/3/2017 7:16	63	5/3/2017 16:21	65	6/3/2017 21:26	63	8/3/2017 22:31	64
28/2/2017 21:11	63	2/3/2017 22:16	63	5/3/2017 7:21	64	5/3/2017 16:26	65	6/3/2017 21:31	62	8/3/2017 22:36	64
28/2/2017 21:16	64	2/3/2017 22:21	63	5/3/2017 7:26	65	5/3/2017 16:31	65	6/3/2017 21:36	63	8/3/2017 22:41	64
28/2/2017 21:21	63	2/3/2017 22:26	63	5/3/2017 7:31	64	5/3/2017 16:36	66	6/3/2017 21:41	63	8/3/2017 22:46	64
28/2/2017 21:26	63	2/3/2017 22:31	64	5/3/2017 7:36	65	5/3/2017 16:41	66	6/3/2017 21:46	62	8/3/2017 22:51	64
28/2/2017 21:31	63	2/3/2017 22:36	63	5/3/2017 7:41	64	5/3/2017 16:46	65	6/3/2017 21:51	63	8/3/2017 22:56	64
28/2/2017 21:36	65	2/3/2017 22:41	63	5/3/2017 7:46	64	5/3/2017 16:51	65	6/3/2017 21:56	63	9/3/2017 19:01	65
28/2/2017 21:41	64	2/3/2017 22:46	63	5/3/2017 7:51	64	5/3/2017 16:56	66	6/3/2017 22:01	63	9/3/2017 19:06	65
28/2/2017 21:46	63	2/3/2017 22:51	63	5/3/2017 7:56	64	5/3/2017 17:01	66	6/3/2017 22:06	63	9/3/2017 19:11	66
28/2/2017 21:51	64	2/3/2017 22:56	62	5/3/2017 8:01	65	5/3/2017 17:06	65	6/3/2017 22:11	63	9/3/2017 19:16	66
28/2/2017 21:56	63	3/3/2017 19:01	66	5/3/2017 8:06	64	5/3/2017 17:11	66	6/3/2017 22:16	64	9/3/2017 19:21	66
28/2/2017 22:01	65	3/3/2017 19:06	66	5/3/2017 8:11	64	5/3/2017 17:16	65	6/3/2017 22:21	63	9/3/2017 19:26	66
28/2/2017 22:06	63	3/3/2017 19:11	67	5/3/2017 8:16	64	5/3/2017 17:21	65	6/3/2017 22:26	63	9/3/2017 19:31	66
28/2/2017 22:11	64	3/3/2017 19:16	65	5/3/2017 8:21	64	5/3/2017 17:26	65	6/3/2017 22:31	63	9/3/2017 19:36	66
28/2/2017 22:16	65	3/3/2017 19:21	65	5/3/2017 8:26	65	5/3/2017 17:31	66	6/3/2017 22:36	63	9/3/2017 19:41	65
28/2/2017 22:21	63	3/3/2017 19:26	65	5/3/2017 8:31	65	5/3/2017 17:36	66	6/3/2017 22:41	63	9/3/2017 19:46	65
28/2/2017 22:26	65	3/3/2017 19:31	65	5/3/2017 8:36	65	5/3/2017 17:41	66	6/3/2017 22:46	63	9/3/2017 19:51	65
28/2/2017 22:31	63	3/3/2017 19:36	64	5/3/2017 8:41	65	5/3/2017 17:46	66	6/3/2017 22:51	63	9/3/2017 19:56	65
28/2/2017 22:36	63	3/3/2017 19:41	65	5/3/2017 8:46	65	5/3/2017 17:51	64	6/3/2017 22:56	63	9/3/2017 20:01	65
28/2/2017 22:41	63	3/3/2017 19:46	64	5/3/2017 8:51	65	5/3/2017 17:56	64	7/3/2017 19:01	64	9/3/2017 20:06	65
28/2/2017 22:46	64	3/3/2017 19:51	65	5/3/2017 8:56	65	5/3/2017 18:01	64	7/3/2017 19:06	65	9/3/2017 20:11	65
28/2/2017 22:51	63	3/3/2017 19:56	63	5/3/2017 9:01	64	5/3/2017 18:06	64	7/3/2017 19:11	65	9/3/2017 20:16	65
28/2/2017 22:56	63	3/3/2017 20:01	64	5/3/2017 9:06	64	5/3/2017 18:11	63	7/3/2017 19:16	65	9/3/2017 20:21	65
1/3/2017 19:01	65	3/3/2017 20:06	64	5/3/2017 9:11	65	5/3/2017 18:16	63	7/3/2017 19:21	65	9/3/2017 20:26	65
1/3/2017 19:06	66	3/3/2017 20:11	65	5/3/2017 9:16	64	5/3/2017 18:21	64	7/3/2017 19:26	65	9/3/2017 20:31	65
1/3/2017 19:11	66	3/3/2017 20:16	64	5/3/2017 9:21	64	5/3/2017 18:26	63	7/3/2017 19:31	65	9/3/2017 20:36	65
1/3/2017 19:16	66	3/3/2017 20:21	64	5/3/2017 9:26	64	5/3/2017 18:31	64	7/3/2017 19:36	64	9/3/2017 20:41	65
1/3/2017 19:21	66	3/3/2017 20:26	64	5/3/2017 9:31	64	5/3/2017 18:36	63	7/3/2017 19:41	65	9/3/2017 20:46	65
1/3/2017 19:26	66	3/3/2017 20:31	64	5/3/2017 9:36	63	5/3/2017 18:41	64	7/3/2017 19:46	63	9/3/2017 20:51	64
1/3/2017 19:31	64	3/3/2017 20:36	63	5/3/2017 9:41	63	5/3/2017 18:46	64	7/3/2017 19:51	64	9/3/2017 20:56	65
1/3/2017 19:36	64	3/3/2017 20:41	63	5/3/2017 9:46	63	5/3/2017 18:51	63	7/3/2017 19:56	64	9/3/2017 21:01	65
1/3/2017 19:41	64	3/3/2017 20:46	64	5/3/2017 9:51	62	5/3/2017 18:56	63	7/3/2017 20:01	64	9/3/2017 21:06	65
1/3/2017 19:46	64	3/3/2017 20:51	64	5/3/2017 9:56	64	5/3/2017 19:01	63	7/3/2017 20:06	64	9/3/2017 21:11	64
1/3/2017 19:51	64	3/3/2017 20:56	63	5/3/2017 10:01	65	5/3/2017 19:06	63	7/3/2017 20:11	64	9/3/2017 21:16	64
1/3/2017 19:56	63	3/3/2017 21:01	63	5/3/2017 10:06	65	5/3/2017 19:11	63	7/3/2017 20:16	64	9/3/2017 21:21	64
1/3/2017 20:01	64	3/3/2017 21:06	63	5/3/2017 10:11	64	5/3/2017 19:16	63	7/3/2017 20:21	63	9/3/2017 21:26	64
1/3/2017 20:06	63	3/3/2017 21:11	63	5/3/2017 10:16	64	5/3/2017 19:21	62	7/3/2017 20:26	64	9/3/2017 21:31	64
1/3/2017 20:11	63	3/3/2017 21:16	67	5/3/2017 10:21	64	5/3/2017 19:26	63	7/3/2017 20:31	63	9/3/2017 21:36	64
1/3/2017 20:16	63	3/3/2017 21:21	64	5/3/2017 10:26	64	5/3/2017 19:31	63	7/3/2017 20:36	63	9/3/2017 21:41	64
1/3/2017 20:21	63	3/3/2017 21:26	63	5/3/2017 10:31	64	5/3/2017 19:36	63	7/3/2017 20:41	64	9/3/2017 21:46	64
1/3/2017 20:26	63	3/3/2017 21:31	63	5/3/2017 10:36	65	5/3/2017 19:41	62	7/3/2017 20:46	63	9/3/2017 21:51	64
1/3/2017 20:31	63	3/3/2017 21:36	63	5/3/2017 10:41	64	5/3/2017 19:46	63	7/3/2017 20:51	63	9/3/2017 21:56	64
1/3/2017 20:36	63	3/3/2017 21:41	64	5/3/2017 10:46	64	5/3/2017 19:51	63	7/3/2017 20:56	64	9/3/2017 22:01	64
1/3/2017 20:41	63	3/3/2017 21:46	64	5/3/2017 10:51	64	5/3/2017 19:56	62	7/3/2017 21:01	63	9/3/2017 22:06	64
1/3/2017 20:46	63	3/3/2017 21:51	62	5/3/2017 10:56	64	5/3/2017 20:01	62	7/3/2017 21:06	63	9/3/2017 22:11	64
1/3/2017 20:51	64	3/3/2017 21:56	64	5/3/2017 11:01	63	5/3/2017 20:06	62	7/3/2017 21:11	63	9/3/2017 22:16	64
1/3/2017 20:56	63	3/3/2017 22:01	63	5/3/2017 11:06	63	5/3/2017 20:11	62	7/3/2017 21:16	63	9/3/2017 22:21	65
1/3/2017 21:01	63	3/3/2017 22:06	63	5/3/2017 11:11	63	5/3/2017 20:16	63	7/3/2017 21:21	63	9/3/2017 22:26	65
1/3/2017 21:06	62	3/3/2017 22:11	64	5/3/2017 11:16	63	5/3/2017 20:21	62	7/3/2017 21:26	63	9/3/2017 22:31	64
1/3/2017 21:11	63	3/3/2017 22:16	64	5/3/2017 11:21	64	5/3/2017 20:26	62	7/3/2017 21:31	62	9/3/2017 22:36	64
1/3/2017 21:16	63	3/3/2017 22:21	63	5/3/2017 11:26	64	5/3/2017 20:31	62	7/3/2017 21:36	63	9/3/2017 22:41	64
1/3/2017 21:21	63	3/3/2017 22:26	63	5/3/2017 11:31	63	5/3/2017 20:36	62	7/3/2017 21:41	63	9/3/2017 22:46	64
1/3/2017 21:26	62	3/3/2017 22:31	64	5/3/2017 11:36	63	5/3/2017 20:41	62	7/3/2017 21:46	63	9/3/2017 22:51	65
1/3/2017 21:31	63	3/3/2017 22:36	64	5/3/2017 11:41	64	5/3/2017 20:46	63	7/3/2017 21:51	63	9/3/2017 22:56	64
1/3/2017 21:36	63	3/3/2017 22:41	64	5/3/2017 11:46	63	5/3/2017 20:51	62	7/3/2017 21:56	64	10/3/2017 19:01	64
1/3/2017 21:41	63	3/3/2017 22:46	64	5/3/2017 11:51	64	5/3/2017 20:56	62	7/3/2017 22:01	63	10/3/2017 19:06	65
1/3/2017 21:46	63	3/3/2017 22:51	66	5/3/2017 11:56	63	5/3/2017 21:01	62	7/3/2017 22:06	62	10/3/2017 19:11	64
1/3/2017 21:51	63	3/3/2017 22:56	63	5/3/2017 12:01	63	5/3/2017 21:06	63	7/3/2017 22:11	63	10/3/2017 19:16	66
1/3/2017 21:56	62	4/3/2017 19:01	66	5/3/2017 12:06	63	5/3/2017 21:11	62	7/3/2017 22:16	63	10/3/2017 19:21	66
1/3/2017 22:01	63	4/3/2017 19:06	65	5/3/2017 12:11	63	5/3/2017 21:16	62	7/3/2017 22:21	64	10/3/2017 19:26	66
1/3/2017 22:06	63	4/3/2017 19:11	65	5/3/2017 12:16	64	5/3/2017 21:21	62	7/3/2017 22:26	64	10/3/2017 19:31	65
1/3/2017 22:11	64	4/3/2017 19:16	65	5/3/2017 12:21	63	5/3/2017 21:26	62	7/3/2017 22:31	63	10/3/2017 19:36	64
1/3/2017 22:16	63	4/3/2017 19:21	65	5/3/2017 12:26	63	5/3/2017 21:31	62	7/3/2017 22:36	64	10/3/2017 19:41	64
1/3/2017 22:21	64	4/3/2017 19:26	65	5/3/2017 12:31	64	5/3/2017 21:36	62	7/3/2017 22:41	64	10/3/2017 19:46	64
1/3/2017 22:26	62	4/3/2017 19:31	65	5/3/2017 12:36	64	5/3/2017 21:41	62	7/3/2017 22:46	65	10/3/2017 19:51	64
1/3/2017 22:31	66	4/3/2017 19:36	65	5/3/2017 12:41	64	5/3/2017 21:46	62	7/3/2017 22:51	63	10/3/2017 19:56	64
1/3/2017 22:36	63	4/3/2017 19:41	65	5/3/2017 12:46	65	5/3/2017 21:51	62	7/3/2017 22:56	62	10/3/2017 20:01	64
1/3/2017 22:41	63	4/3/2017 19:46	65	5/3/2017 12:51	64	5/3/2017 21:56	62	8/3/2017 19:01	67	10/3/2017 20:06	64
1/3/2017 22:46	63	4/3/2017 19:51	65	5/3/2017 12:56	64	5/3/2017 22:01	62	8/3/2017 19:06	65	10/3/2017 20:11	64
1/3/2017 22:51	63	4/3/2017 19:56	64	5/3/2017 13:01	63	5/3/2017 22:06	62	8/3/2017 19:11	65	10/3/2017 20:16	64
1/3/2017 22:56	63	4/3/2017 20:01	65	5/3/2017 13:06	64	5/3/2017 22:11	62	8/3/2017 19:16	66	10/3/2017 20:21	64
2/3/2017 19:01	65	4/3/2017 20:06	65	5/3/2017 13:11	63	5/3/2017 22:16	63	8/3/2017 19:21	66	10/3/2017 20:26	63
2/3/2017 19:06	65	4/3/2017 20:11	64	5/3/2017 13:16	63	5/3/2017 22:21	62	8/3/2017 19:26	66	10/3/2017 20:31	63
2/3/2017 19:11	65	4/3/2017 20:16	64	5/3/2017 13:21	63	5/3/2017 22:26	61	8/3/2017 19:31	66	10/3/2	

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
11/3/2017 19:26	65	12/3/2017 12:31	64	12/3/2017 21:36	63	14/3/2017 22:41	63	17/3/2017 19:46	65	19/3/2017 8:51	65
11/3/2017 19:31	64	12/3/2017 12:36	64	12/3/2017 21:41	63	14/3/2017 22:46	63	17/3/2017 19:51	66	19/3/2017 8:56	64
11/3/2017 19:36	64	12/3/2017 12:41	65	12/3/2017 21:46	63	14/3/2017 22:51	63	17/3/2017 19:56	65	19/3/2017 9:01	64
11/3/2017 19:41	64	12/3/2017 12:46	64	12/3/2017 21:51	63	14/3/2017 22:56	63	17/3/2017 20:01	65	19/3/2017 9:06	64
11/3/2017 19:46	64	12/3/2017 12:51	65	12/3/2017 21:56	63	15/3/2017 19:01	66	17/3/2017 20:06	65	19/3/2017 9:11	65
11/3/2017 19:51	63	12/3/2017 12:56	64	12/3/2017 22:01	63	15/3/2017 19:06	66	17/3/2017 20:11	66	19/3/2017 9:16	64
11/3/2017 19:56	64	12/3/2017 13:01	64	12/3/2017 22:06	63	15/3/2017 19:11	66	17/3/2017 20:16	65	19/3/2017 9:21	64
11/3/2017 20:01	63	12/3/2017 13:06	64	12/3/2017 22:11	63	15/3/2017 19:16	66	17/3/2017 20:21	66	19/3/2017 9:26	63
11/3/2017 20:06	64	12/3/2017 13:11	64	12/3/2017 22:16	63	15/3/2017 19:21	66	17/3/2017 20:26	65	19/3/2017 9:31	63
11/3/2017 20:11	63	12/3/2017 13:16	64	12/3/2017 22:21	64	15/3/2017 19:26	66	17/3/2017 20:31	65	19/3/2017 9:36	64
11/3/2017 20:16	63	12/3/2017 13:21	64	12/3/2017 22:26	63	15/3/2017 19:31	65	17/3/2017 20:36	66	19/3/2017 9:41	64
11/3/2017 20:21	63	12/3/2017 13:26	64	12/3/2017 22:31	63	15/3/2017 19:36	65	17/3/2017 20:41	65	19/3/2017 9:46	65
11/3/2017 20:26	63	12/3/2017 13:31	64	12/3/2017 22:36	63	15/3/2017 19:41	65	17/3/2017 20:46	65	19/3/2017 9:51	66
11/3/2017 20:31	64	12/3/2017 13:36	64	12/3/2017 22:41	63	15/3/2017 19:46	65	17/3/2017 20:51	65	19/3/2017 9:56	65
11/3/2017 20:36	64	12/3/2017 13:41	65	12/3/2017 22:46	62	15/3/2017 19:51	65	17/3/2017 20:56	65	19/3/2017 10:01	64
11/3/2017 20:41	62	12/3/2017 13:46	64	12/3/2017 22:51	62	15/3/2017 19:56	65	17/3/2017 21:01	65	19/3/2017 10:06	64
11/3/2017 20:46	63	12/3/2017 13:51	65	12/3/2017 22:56	62	15/3/2017 20:01	64	17/3/2017 21:06	65	19/3/2017 10:11	65
11/3/2017 20:51	63	12/3/2017 13:56	65	13/3/2017 19:01	66	15/3/2017 20:06	65	17/3/2017 21:11	65	19/3/2017 10:16	66
11/3/2017 20:56	63	12/3/2017 14:01	64	13/3/2017 19:06	65	15/3/2017 20:11	65	17/3/2017 21:16	65	19/3/2017 10:21	65
11/3/2017 21:01	63	12/3/2017 14:06	65	13/3/2017 19:11	65	15/3/2017 20:16	64	17/3/2017 21:21	65	19/3/2017 10:26	66
11/3/2017 21:06	63	12/3/2017 14:11	65	13/3/2017 19:16	66	15/3/2017 20:21	64	17/3/2017 21:26	65	19/3/2017 10:31	64
11/3/2017 21:11	63	12/3/2017 14:16	64	13/3/2017 19:21	66	15/3/2017 20:26	65	17/3/2017 21:31	65	19/3/2017 10:36	66
11/3/2017 21:16	64	12/3/2017 14:21	65	13/3/2017 19:26	66	15/3/2017 20:31	64	17/3/2017 21:36	65	19/3/2017 10:41	67
11/3/2017 21:21	64	12/3/2017 14:26	65	13/3/2017 19:31	64	15/3/2017 20:36	64	17/3/2017 21:41	65	19/3/2017 10:46	65
11/3/2017 21:26	63	12/3/2017 14:31	64	13/3/2017 19:36	64	15/3/2017 20:41	63	17/3/2017 21:46	65	19/3/2017 10:51	64
11/3/2017 21:31	63	12/3/2017 14:36	64	13/3/2017 19:41	64	15/3/2017 20:46	64	17/3/2017 21:51	65	19/3/2017 10:56	64
11/3/2017 21:36	63	12/3/2017 14:41	64	13/3/2017 19:46	64	15/3/2017 20:51	64	17/3/2017 21:56	65	19/3/2017 11:01	64
11/3/2017 21:41	63	12/3/2017 14:46	64	13/3/2017 19:51	65	15/3/2017 20:56	64	17/3/2017 22:01	65	19/3/2017 11:06	65
11/3/2017 21:46	63	12/3/2017 14:51	63	13/3/2017 19:56	63	15/3/2017 21:01	64	17/3/2017 22:06	65	19/3/2017 11:11	64
11/3/2017 21:51	64	12/3/2017 14:56	64	13/3/2017 20:01	64	15/3/2017 21:06	63	17/3/2017 22:11	65	19/3/2017 11:16	63
11/3/2017 21:56	63	12/3/2017 15:01	63	13/3/2017 20:06	66	15/3/2017 21:11	64	17/3/2017 22:16	65	19/3/2017 11:21	64
11/3/2017 22:01	64	12/3/2017 15:06	64	13/3/2017 20:11	63	15/3/2017 21:16	63	17/3/2017 22:21	65	19/3/2017 11:26	64
11/3/2017 22:06	63	12/3/2017 15:11	64	13/3/2017 20:16	65	15/3/2017 21:21	64	17/3/2017 22:26	65	19/3/2017 11:31	63
11/3/2017 22:11	63	12/3/2017 15:16	63	13/3/2017 20:21	63	15/3/2017 21:26	63	17/3/2017 22:31	65	19/3/2017 11:36	64
11/3/2017 22:16	64	12/3/2017 15:21	64	13/3/2017 20:26	63	15/3/2017 21:31	63	17/3/2017 22:36	66	19/3/2017 11:41	65
11/3/2017 22:21	63	12/3/2017 15:26	65	13/3/2017 20:31	64	15/3/2017 21:36	63	17/3/2017 22:41	65	19/3/2017 11:46	65
11/3/2017 22:26	63	12/3/2017 15:31	65	13/3/2017 20:36	64	15/3/2017 21:41	64	17/3/2017 22:46	65	19/3/2017 11:51	65
11/3/2017 22:31	64	12/3/2017 15:36	64	13/3/2017 20:41	63	15/3/2017 21:46	64	17/3/2017 22:51	65	19/3/2017 11:56	65
11/3/2017 22:36	63	12/3/2017 15:41	64	13/3/2017 20:46	64	15/3/2017 21:51	64	17/3/2017 22:56	65	19/3/2017 12:01	65
11/3/2017 22:41	63	12/3/2017 15:46	65	13/3/2017 20:51	64	15/3/2017 21:56	63	18/3/2017 19:01	64	19/3/2017 12:06	66
11/3/2017 22:46	63	12/3/2017 15:51	64	13/3/2017 20:56	63	15/3/2017 22:01	63	18/3/2017 19:06	63	19/3/2017 12:11	66
11/3/2017 22:51	62	12/3/2017 15:56	65	13/3/2017 21:01	63	15/3/2017 22:06	64	18/3/2017 19:11	63	19/3/2017 12:16	66
11/3/2017 22:56	62	12/3/2017 16:01	65	13/3/2017 21:06	63	15/3/2017 22:11	64	18/3/2017 19:16	63	19/3/2017 12:21	66
12/3/2017 7:01	62	12/3/2017 16:06	65	13/3/2017 21:11	63	15/3/2017 22:16	64	18/3/2017 19:21	63	19/3/2017 12:26	66
12/3/2017 7:06	63	12/3/2017 16:11	65	13/3/2017 21:16	63	15/3/2017 22:21	64	18/3/2017 19:26	62	19/3/2017 12:31	66
12/3/2017 7:11	63	12/3/2017 16:16	65	13/3/2017 21:21	63	15/3/2017 22:26	64	18/3/2017 19:31	62	19/3/2017 12:36	66
12/3/2017 7:16	62	12/3/2017 16:21	65	13/3/2017 21:26	63	15/3/2017 22:31	64	18/3/2017 19:36	62	19/3/2017 12:41	67
12/3/2017 7:21	63	12/3/2017 16:26	65	13/3/2017 21:31	63	15/3/2017 22:36	64	18/3/2017 19:41	63	19/3/2017 12:46	66
12/3/2017 7:26	63	12/3/2017 16:31	67	13/3/2017 21:36	63	15/3/2017 22:41	63	18/3/2017 19:46	63	19/3/2017 12:51	65
12/3/2017 7:31	63	12/3/2017 16:36	67	13/3/2017 21:41	63	15/3/2017 22:46	63	18/3/2017 19:51	62	19/3/2017 12:56	68
12/3/2017 7:36	63	12/3/2017 16:41	66	13/3/2017 21:46	63	15/3/2017 22:51	62	18/3/2017 19:56	63	19/3/2017 13:01	68
12/3/2017 7:41	63	12/3/2017 16:46	67	13/3/2017 21:51	63	15/3/2017 22:56	63	18/3/2017 20:01	63	19/3/2017 13:06	67
12/3/2017 7:46	63	12/3/2017 16:51	67	13/3/2017 21:56	63	16/3/2017 19:01	66	18/3/2017 20:06	64	19/3/2017 13:11	67
12/3/2017 7:51	63	12/3/2017 16:56	66	13/3/2017 22:01	63	16/3/2017 19:06	66	18/3/2017 20:11	63	19/3/2017 13:16	62
12/3/2017 7:56	64	12/3/2017 17:01	66	13/3/2017 22:06	64	16/3/2017 19:11	66	18/3/2017 20:16	63	19/3/2017 13:21	62
12/3/2017 8:01	63	12/3/2017 17:06	66	13/3/2017 22:11	63	16/3/2017 19:16	66	18/3/2017 20:21	63	19/3/2017 13:26	67
12/3/2017 8:06	63	12/3/2017 17:11	68	13/3/2017 22:16	63	16/3/2017 19:21	67	18/3/2017 20:26	63	19/3/2017 13:31	69
12/3/2017 8:11	64	12/3/2017 17:16	65	13/3/2017 22:21	63	16/3/2017 19:26	66	18/3/2017 20:31	62	19/3/2017 13:36	68
12/3/2017 8:16	64	12/3/2017 17:21	66	13/3/2017 22:26	63	16/3/2017 19:31	65	18/3/2017 20:36	63	19/3/2017 13:41	65
12/3/2017 8:21	64	12/3/2017 17:26	66	13/3/2017 22:31	63	16/3/2017 19:36	65	18/3/2017 20:41	63	19/3/2017 13:46	65
12/3/2017 8:26	64	12/3/2017 17:31	66	13/3/2017 22:36	64	16/3/2017 19:41	65	18/3/2017 20:46	63	19/3/2017 13:51	66
12/3/2017 8:31	64	12/3/2017 17:36	65	13/3/2017 22:41	63	16/3/2017 19:46	64	18/3/2017 20:51	63	19/3/2017 13:56	66
12/3/2017 8:36	65	12/3/2017 17:41	64	13/3/2017 22:46	63	16/3/2017 19:51	65	18/3/2017 20:56	63	19/3/2017 14:01	66
12/3/2017 8:41	64	12/3/2017 17:46	65	13/3/2017 22:51	63	16/3/2017 19:56	65	18/3/2017 21:01	63	19/3/2017 14:06	66
12/3/2017 8:46	64	12/3/2017 17:51	64	13/3/2017 22:56	63	16/3/2017 20:01	65	18/3/2017 21:06	63	19/3/2017 14:11	66
12/3/2017 8:51	65	12/3/2017 17:56	65	14/3/2017 19:01	66	16/3/2017 20:06	64	18/3/2017 21:11	63	19/3/2017 14:16	66
12/3/2017 8:56	65	12/3/2017 18:01	65	14/3/2017 19:06	66	16/3/2017 20:11	65	18/3/2017 21:16	63	19/3/2017 14:21	65
12/3/2017 9:01	64	12/3/2017 18:06	65	14/3/2017 19:11	66	16/3/2017 20:16	65	18/3/2017 21:21	63	19/3/2017 14:26	64
12/3/2017 9:06	65	12/3/2017 18:11	64	14/3/2017 19:16	66	16/3/2017 20:21	64	18/3/2017 21:26	65	19/3/2017 14:31	65
12/3/2017 9:11	64	12/3/2017 18:16	64	14/3/2017 19:21	66	16/3/2017 20:26	64	18/3/2017 21:31	63	19/3/2017 14:36	64
12/3/2017 9:16	65	12/3/2017 18:21	65	14/3/2017 19:26	65	16/3/2017 20:31	64	18/3/2017 21:36	63	19/3/2017 14:41	65
12/3/2017 9:21	65	12/3/2017 18:26	65	14/3/2017 19:31	65	16/3/2017 20:36	64	18/3/2017 21:41	63	19/3/2017 14:46	65
12/3/2017 9:26	65	12/3/2017 18:31	64	14/3/2017 19:36	65	16/3/2017 20:41	64	18/3/2017 21:46	64	19/3/2017 14:51	65
12/3/2017 9:31	65	12/3/2017 18:36	64	14/3/2017 19:41							

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)						Night time: 23:00-07:00	
19/3/2017 17:56	65	21/3/2017 19:01	66	23/3/2017 20:06	64	25/3/2017 21:11	63	26/3/2017 14:16	66
19/3/2017 18:01	65	21/3/2017 19:06	65	23/3/2017 20:11	65	25/3/2017 21:16	63	26/3/2017 14:21	66
19/3/2017 18:06	65	21/3/2017 19:11	65	23/3/2017 20:16	64	25/3/2017 21:21	63	26/3/2017 14:26	65
19/3/2017 18:11	65	21/3/2017 19:16	65	23/3/2017 20:21	64	25/3/2017 21:26	63	26/3/2017 14:31	65
19/3/2017 18:16	64	21/3/2017 19:21	65	23/3/2017 20:26	65	25/3/2017 21:31	63	26/3/2017 14:36	65
19/3/2017 18:21	65	21/3/2017 19:26	65	23/3/2017 20:31	64	25/3/2017 21:36	63	26/3/2017 14:41	65
19/3/2017 18:26	65	21/3/2017 19:31	65	23/3/2017 20:36	64	25/3/2017 21:41	63	26/3/2017 14:46	65
19/3/2017 18:31	65	21/3/2017 19:36	64	23/3/2017 20:41	64	25/3/2017 21:46	63	26/3/2017 14:51	66
19/3/2017 18:36	65	21/3/2017 19:41	64	23/3/2017 20:46	64	25/3/2017 21:51	63	26/3/2017 14:56	65
19/3/2017 18:41	65	21/3/2017 19:46	64	23/3/2017 20:51	63	25/3/2017 21:56	63	26/3/2017 15:01	65
19/3/2017 18:46	65	21/3/2017 19:51	64	23/3/2017 20:56	64	25/3/2017 22:01	63	26/3/2017 15:06	65
19/3/2017 18:51	65	21/3/2017 19:56	64	23/3/2017 21:01	64	25/3/2017 22:06	63	26/3/2017 15:11	66
19/3/2017 18:56	64	21/3/2017 20:01	64	23/3/2017 21:06	65	25/3/2017 22:11	63	26/3/2017 15:16	65
19/3/2017 19:01	65	21/3/2017 20:06	64	23/3/2017 21:11	63	25/3/2017 22:16	63	26/3/2017 15:21	66
19/3/2017 19:06	65	21/3/2017 20:11	64	23/3/2017 21:16	66	25/3/2017 22:21	63	26/3/2017 15:26	65
19/3/2017 19:11	65	21/3/2017 20:16	64	23/3/2017 21:21	63	25/3/2017 22:26	63	26/3/2017 15:31	64
19/3/2017 19:16	64	21/3/2017 20:21	64	23/3/2017 21:26	64	25/3/2017 22:31	63	26/3/2017 15:36	65
19/3/2017 19:21	64	21/3/2017 20:26	63	23/3/2017 21:31	64	25/3/2017 22:36	64	26/3/2017 15:41	65
19/3/2017 19:26	64	21/3/2017 20:31	63	23/3/2017 21:36	64	25/3/2017 22:41	64	26/3/2017 15:46	65
19/3/2017 19:31	64	21/3/2017 20:36	65	23/3/2017 21:41	63	25/3/2017 22:46	63	26/3/2017 15:51	66
19/3/2017 19:36	64	21/3/2017 20:41	63	23/3/2017 21:46	64	25/3/2017 22:51	63	26/3/2017 15:56	67
19/3/2017 19:41	65	21/3/2017 20:46	63	23/3/2017 21:51	64	25/3/2017 22:56	63	26/3/2017 16:01	68
19/3/2017 19:46	64	21/3/2017 20:51	64	23/3/2017 21:56	63	26/3/2017 7:01	61	26/3/2017 16:06	68
19/3/2017 19:51	64	21/3/2017 20:56	63	23/3/2017 22:01	63	26/3/2017 7:06	62	26/3/2017 16:11	67
19/3/2017 19:56	64	21/3/2017 21:01	63	23/3/2017 22:06	64	26/3/2017 7:11	61	26/3/2017 16:16	67
19/3/2017 20:01	64	21/3/2017 21:06	62	23/3/2017 22:11	64	26/3/2017 7:16	61	26/3/2017 16:21	67
19/3/2017 20:06	64	21/3/2017 21:11	63	23/3/2017 22:16	64	26/3/2017 7:21	61	26/3/2017 16:26	68
19/3/2017 20:11	64	21/3/2017 21:16	63	23/3/2017 22:21	63	26/3/2017 7:26	62	26/3/2017 16:31	68
19/3/2017 20:16	64	21/3/2017 21:21	63	23/3/2017 22:26	64	26/3/2017 7:31	63	26/3/2017 16:36	67
19/3/2017 20:21	65	21/3/2017 21:26	62	23/3/2017 22:31	64	26/3/2017 7:36	62	26/3/2017 16:41	67
19/3/2017 20:26	64	21/3/2017 21:31	63	23/3/2017 22:36	63	26/3/2017 7:41	63	26/3/2017 16:46	67
19/3/2017 20:31	64	21/3/2017 21:36	62	23/3/2017 22:41	64	26/3/2017 7:46	62	26/3/2017 16:51	67
19/3/2017 20:36	65	21/3/2017 21:41	62	23/3/2017 22:46	64	26/3/2017 7:51	62	26/3/2017 16:56	66
19/3/2017 20:41	63	21/3/2017 21:46	63	23/3/2017 22:51	63	26/3/2017 7:56	62	26/3/2017 17:01	67
19/3/2017 20:46	64	21/3/2017 21:51	62	23/3/2017 22:56	63	26/3/2017 8:01	62	26/3/2017 17:06	67
19/3/2017 20:51	64	21/3/2017 21:56	62	24/3/2017 19:01	64	26/3/2017 8:06	63	26/3/2017 17:11	67
19/3/2017 20:56	64	21/3/2017 22:01	62	24/3/2017 19:06	65	26/3/2017 8:11	63	26/3/2017 17:16	67
19/3/2017 21:01	64	21/3/2017 22:06	62	24/3/2017 19:11	66	26/3/2017 8:16	63	26/3/2017 17:21	66
19/3/2017 21:06	64	21/3/2017 22:11	63	24/3/2017 19:16	65	26/3/2017 8:21	63	26/3/2017 17:26	67
19/3/2017 21:11	64	21/3/2017 22:16	63	24/3/2017 19:21	66	26/3/2017 8:26	64	26/3/2017 17:31	66
19/3/2017 21:16	64	21/3/2017 22:21	64	24/3/2017 19:26	66	26/3/2017 8:31	64	26/3/2017 17:36	66
19/3/2017 21:21	64	21/3/2017 22:26	63	24/3/2017 19:31	64	26/3/2017 8:36	64	26/3/2017 17:41	67
19/3/2017 21:26	64	21/3/2017 22:31	63	24/3/2017 19:36	64	26/3/2017 8:41	64	26/3/2017 17:46	67
19/3/2017 21:31	64	21/3/2017 22:36	63	24/3/2017 19:41	64	26/3/2017 8:46	65	26/3/2017 17:51	67
19/3/2017 21:36	64	21/3/2017 22:41	62	24/3/2017 19:46	65	26/3/2017 8:51	65	26/3/2017 17:56	66
19/3/2017 21:41	63	21/3/2017 22:46	62	24/3/2017 19:51	64	26/3/2017 8:56	65	26/3/2017 18:01	67
19/3/2017 21:46	64	21/3/2017 22:51	63	24/3/2017 19:56	65	26/3/2017 9:01	64	26/3/2017 18:06	67
19/3/2017 21:51	64	21/3/2017 22:56	63	24/3/2017 20:01	64	26/3/2017 9:06	66	26/3/2017 18:11	66
19/3/2017 21:56	64	22/3/2017 19:01	66	24/3/2017 20:06	64	26/3/2017 9:11	65	26/3/2017 18:16	66
19/3/2017 22:01	64	22/3/2017 19:06	66	24/3/2017 20:11	64	26/3/2017 9:16	65	26/3/2017 18:21	66
19/3/2017 22:06	64	22/3/2017 19:11	66	24/3/2017 20:16	64	26/3/2017 9:21	65	26/3/2017 18:26	66
19/3/2017 22:11	64	22/3/2017 19:16	66	24/3/2017 20:21	64	26/3/2017 9:26	66	26/3/2017 18:31	65
19/3/2017 22:16	64	22/3/2017 19:21	67	24/3/2017 20:26	63	26/3/2017 9:31	66	26/3/2017 18:36	66
19/3/2017 22:21	64	22/3/2017 19:26	66	24/3/2017 20:31	63	26/3/2017 9:36	67	26/3/2017 18:41	65
19/3/2017 22:26	64	22/3/2017 19:31	65	24/3/2017 20:36	64	26/3/2017 9:41	67	26/3/2017 18:46	65
19/3/2017 22:31	63	22/3/2017 19:36	65	24/3/2017 20:41	64	26/3/2017 9:46	68	26/3/2017 18:51	65
19/3/2017 22:36	63	22/3/2017 19:41	65	24/3/2017 20:46	63	26/3/2017 9:51	68	26/3/2017 18:56	64
19/3/2017 22:41	64	22/3/2017 19:46	64	24/3/2017 20:51	63	26/3/2017 9:56	66	26/3/2017 19:01	65
19/3/2017 22:46	63	22/3/2017 19:51	64	24/3/2017 20:56	63	26/3/2017 10:01	66	26/3/2017 19:06	65
19/3/2017 22:51	63	22/3/2017 19:56	64	24/3/2017 21:01	63	26/3/2017 10:06	65	26/3/2017 19:11	65
19/3/2017 22:56	63	22/3/2017 20:01	64	24/3/2017 21:06	64	26/3/2017 10:11	67	26/3/2017 19:16	64
20/3/2017 19:01	64	22/3/2017 20:06	64	24/3/2017 21:11	64	26/3/2017 10:16	67	26/3/2017 19:21	65
20/3/2017 19:06	64	22/3/2017 20:11	65	24/3/2017 21:16	64	26/3/2017 10:21	67	26/3/2017 19:26	65
20/3/2017 19:11	64	22/3/2017 20:16	66	24/3/2017 21:21	63	26/3/2017 10:26	66	26/3/2017 19:31	64
20/3/2017 19:16	64	22/3/2017 20:21	65	24/3/2017 21:26	62	26/3/2017 10:31	65	26/3/2017 19:36	64
20/3/2017 19:21	64	22/3/2017 20:26	63	24/3/2017 21:31	63	26/3/2017 10:36	64	26/3/2017 19:41	64
20/3/2017 19:26	64	22/3/2017 20:31	64	24/3/2017 21:36	63	26/3/2017 10:41	65	26/3/2017 19:46	63
20/3/2017 19:31	63	22/3/2017 20:36	64	24/3/2017 21:41	63	26/3/2017 10:46	65	26/3/2017 19:51	64
20/3/2017 19:36	62	22/3/2017 20:41	64	24/3/2017 21:46	63	26/3/2017 10:51	64	26/3/2017 19:56	64
20/3/2017 19:41	63	22/3/2017 20:46	63	24/3/2017 21:51	64	26/3/2017 10:56	65	26/3/2017 20:01	64
20/3/2017 19:46	63	22/3/2017 20:51	64	24/3/2017 21:56	64	26/3/2017 11:01	65	26/3/2017 20:06	64
20/3/2017 19:51	63	22/3/2017 20:56	64	24/3/2017 22:01	63	26/3/2017 11:06	65	26/3/2017 20:11	64
20/3/2017 19:56	64	22/3/2017 21:01	64	24/3/2017 22:06	65	26/3/2017 11:11	64	26/3/2017 20:16	64
20/3/2017 20:01	64	22/3/2017 21:06	64	24/3/2017 22:11	64	26/3/2017 11:16	65	26/3/2017 20:21	64
20/3/2017 20:06	65	22/3/2017 21:11	64	24/3/2017 22:16	64	26/3/2017 11:21	65	26/3/2017 20:26	64
20/3/2017 20:11	64	22/3/2017 21:16	64	24/3/2017 22:21	65	26/3/2017 11:26	65	26/3/2017 20:31	65
20/3/2017 20:16	64	22/3/2017 21:21	64	24/3/2017 22:26	63	26/3/2017 11:31	65	26/3/2017 20:36	63
20/3/2017 20:21	64	22/3/2017 21:26	64	24/3/2017 22:31	63	26/3/2017 11:36	65	26/3/2017 20:41	64
20/3/2017 20:26	63	22/3/2017 21:31	65	24/3/2017 22:36	65	26/3/2017 11:41	65	26/3/2017 20:46	63
20/3/2017 20:31	64	22/3/2017 21:36	63	24/3/2017 22:41	64	26/3/2017 11:46	64	26/3/2017 20:51	64
20/3/2017 20:36	66	22/3/2017 21:41	63	24/3/2017 22:46	63	26/3/2017 11:51	66	26/3/2017 20:56	63
20/3/2017 20:41	64	22/3/2017 21:46	64	24/3/2017 22:51	63	26/3/2017 11:56	64	26/3/2017 21:01	63
20/3/2017 20:46	64	22/3/2017 21:51	64	24/3/2017 22:56	63	26/3/2017 12:01	64	26/3/2017 21:06	64
20/3/2017 20:51	64	22/3/2017 21:56	63	25/3/2017 19:01	64	26/3/2017 12:06	65	26/3/2017 21:11	64
20/3/2017 20:56	63	22/3/2017 22:01	65	25/3/2017 19:06	64	26/3/2017 12:11	64	26/3/2017 21:16	64
20/3/2017 21:01	63	22/3/2017 22:06	64	25/3/2017 19:11	63	26/3/2017 12:16	65	26/3/2017 21:21	63
20/3/2017 21:06	64	22/3/2017 22:11	64	25/3/2017 19:16	64	26/3/2017 12:21	66	26/3/2017 21:26	63
20/3/2017 21:11	63	22/3/2017 22:16	63	25/3/2017 19:21					

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
28/2/2017 0:56	61	1/3/2017 2:01	59	2/3/2017 3:06	57	3/3/2017 4:11	59	4/3/2017 5:16	58	5/3/2017 6:21	56
28/2/2017 1:01	59	1/3/2017 2:06	59	2/3/2017 3:11	58	3/3/2017 4:16	57	4/3/2017 5:21	59	5/3/2017 6:26	58
28/2/2017 1:06	62	1/3/2017 2:11	58	2/3/2017 3:16	59	3/3/2017 4:21	57	4/3/2017 5:26	60	5/3/2017 6:31	59
28/2/2017 1:11	60	1/3/2017 2:16	58	2/3/2017 3:21	57	3/3/2017 4:26	57	4/3/2017 5:31	59	5/3/2017 6:36	56
28/2/2017 1:16	59	1/3/2017 2:21	59	2/3/2017 3:26	58	3/3/2017 4:31	57	4/3/2017 5:36	58	5/3/2017 6:41	59
28/2/2017 1:21	59	1/3/2017 2:26	59	2/3/2017 3:31	57	3/3/2017 4:36	56	4/3/2017 5:41	60	5/3/2017 6:46	58
28/2/2017 1:26	60	1/3/2017 2:31	58	2/3/2017 3:36	58	3/3/2017 4:41	57	4/3/2017 5:46	59	5/3/2017 6:51	57
28/2/2017 1:31	60	1/3/2017 2:36	58	2/3/2017 3:41	57	3/3/2017 4:46	58	4/3/2017 5:51	59	5/3/2017 6:56	59
28/2/2017 1:36	59	1/3/2017 2:41	58	2/3/2017 3:46	57	3/3/2017 4:51	57	4/3/2017 5:56	60	5/3/2017 23:01	49
28/2/2017 1:41	60	1/3/2017 2:46	57	2/3/2017 3:51	57	3/3/2017 4:56	58	4/3/2017 6:01	59	5/3/2017 23:06	61
28/2/2017 1:46	59	1/3/2017 2:51	58	2/3/2017 3:56	57	3/3/2017 5:01	58	4/3/2017 6:06	59	5/3/2017 23:11	50
28/2/2017 1:51	59	1/3/2017 2:56	58	2/3/2017 4:01	56	3/3/2017 5:06	59	4/3/2017 6:11	60	5/3/2017 23:16	61
28/2/2017 1:56	58	1/3/2017 3:01	57	2/3/2017 4:06	57	3/3/2017 5:11	57	4/3/2017 6:16	60	5/3/2017 23:21	62
28/2/2017 2:01	59	1/3/2017 3:06	57	2/3/2017 4:11	57	3/3/2017 5:16	57	4/3/2017 6:21	60	5/3/2017 23:26	46
28/2/2017 2:06	58	1/3/2017 3:11	57	2/3/2017 4:16	58	3/3/2017 5:21	59	4/3/2017 6:26	61	5/3/2017 23:31	61
28/2/2017 2:11	58	1/3/2017 3:16	57	2/3/2017 4:21	56	3/3/2017 5:26	58	4/3/2017 6:31	61	5/3/2017 23:36	61
28/2/2017 2:16	58	1/3/2017 3:21	57	2/3/2017 4:26	57	3/3/2017 5:31	58	4/3/2017 6:36	62	5/3/2017 23:41	60
28/2/2017 2:21	58	1/3/2017 3:26	57	2/3/2017 4:31	57	3/3/2017 5:36	58	4/3/2017 6:41	62	5/3/2017 23:46	61
28/2/2017 2:26	59	1/3/2017 3:31	58	2/3/2017 4:36	56	3/3/2017 5:41	59	4/3/2017 6:46	49	5/3/2017 23:51	60
28/2/2017 2:31	58	1/3/2017 3:36	58	2/3/2017 4:41	58	3/3/2017 5:46	60	4/3/2017 6:51	54	5/3/2017 23:56	60
28/2/2017 2:36	58	1/3/2017 3:41	57	2/3/2017 4:46	57	3/3/2017 5:51	59	4/3/2017 6:56	52	6/3/2017 0:01	60
28/2/2017 2:41	58	1/3/2017 3:46	57	2/3/2017 4:51	57	3/3/2017 5:56	59	4/3/2017 23:01	61	6/3/2017 0:06	61
28/2/2017 2:46	58	1/3/2017 3:51	57	2/3/2017 4:56	58	3/3/2017 6:01	59	4/3/2017 23:06	60	6/3/2017 0:11	60
28/2/2017 2:51	57	1/3/2017 3:56	57	2/3/2017 5:01	57	3/3/2017 6:06	61	4/3/2017 23:11	60	6/3/2017 0:16	60
28/2/2017 2:56	57	1/3/2017 4:01	56	2/3/2017 5:06	57	3/3/2017 6:11	61	4/3/2017 23:16	61	6/3/2017 0:21	59
28/2/2017 3:01	58	1/3/2017 4:06	57	2/3/2017 5:11	58	3/3/2017 6:16	61	4/3/2017 23:21	60	6/3/2017 0:26	59
28/2/2017 3:06	58	1/3/2017 4:11	58	2/3/2017 5:16	58	3/3/2017 6:21	61	4/3/2017 23:26	60	6/3/2017 0:31	60
28/2/2017 3:11	58	1/3/2017 4:16	57	2/3/2017 5:21	59	3/3/2017 6:26	53	4/3/2017 23:31	59	6/3/2017 0:36	59
28/2/2017 3:16	57	1/3/2017 4:21	57	2/3/2017 5:26	59	3/3/2017 6:31	62	4/3/2017 23:36	58	6/3/2017 0:41	59
28/2/2017 3:21	58	1/3/2017 4:26	58	2/3/2017 5:31	58	3/3/2017 6:36	58	4/3/2017 23:41	61	6/3/2017 0:46	59
28/2/2017 3:26	59	1/3/2017 4:31	58	2/3/2017 5:36	59	3/3/2017 6:41	57	4/3/2017 23:46	59	6/3/2017 0:51	60
28/2/2017 3:31	57	1/3/2017 4:36	58	2/3/2017 5:41	59	3/3/2017 6:46	58	4/3/2017 23:51	59	6/3/2017 0:56	59
28/2/2017 3:36	58	1/3/2017 4:41	57	2/3/2017 5:46	59	3/3/2017 6:51	60	4/3/2017 23:56	59	6/3/2017 1:01	59
28/2/2017 3:41	57	1/3/2017 4:46	58	2/3/2017 5:51	60	3/3/2017 6:56	58	5/3/2017 0:01	57	6/3/2017 1:06	59
28/2/2017 3:46	57	1/3/2017 4:51	59	2/3/2017 5:56	60	3/3/2017 23:01	58	5/3/2017 0:06	59	6/3/2017 1:11	58
28/2/2017 3:51	58	1/3/2017 4:56	57	2/3/2017 6:01	59	3/3/2017 23:06	57	5/3/2017 0:11	59	6/3/2017 1:16	59
28/2/2017 3:56	58	1/3/2017 5:01	58	2/3/2017 6:06	61	3/3/2017 23:11	56	5/3/2017 0:16	58	6/3/2017 1:21	59
28/2/2017 4:01	56	1/3/2017 5:06	58	2/3/2017 6:11	60	3/3/2017 23:16	60	5/3/2017 0:21	57	6/3/2017 1:26	59
28/2/2017 4:06	57	1/3/2017 5:11	58	2/3/2017 6:16	61	3/3/2017 23:21	56	5/3/2017 0:26	59	6/3/2017 1:31	58
28/2/2017 4:11	58	1/3/2017 5:16	57	2/3/2017 6:21	61	3/3/2017 23:26	55	5/3/2017 0:31	58	6/3/2017 1:36	58
28/2/2017 4:16	57	1/3/2017 5:21	59	2/3/2017 6:26	47	3/3/2017 23:31	54	5/3/2017 0:36	57	6/3/2017 1:41	58
28/2/2017 4:21	57	1/3/2017 5:26	58	2/3/2017 6:31	49	3/3/2017 23:36	54	5/3/2017 0:41	57	6/3/2017 1:46	58
28/2/2017 4:26	58	1/3/2017 5:31	59	2/3/2017 6:36	55	3/3/2017 23:41	56	5/3/2017 0:46	57	6/3/2017 1:51	57
28/2/2017 4:31	57	1/3/2017 5:36	59	2/3/2017 6:41	58	3/3/2017 23:46	42	5/3/2017 0:51	56	6/3/2017 1:56	57
28/2/2017 4:36	57	1/3/2017 5:41	60	2/3/2017 6:46	57	3/3/2017 23:51	62	5/3/2017 0:56	57	6/3/2017 2:01	57
28/2/2017 4:41	57	1/3/2017 5:46	60	2/3/2017 6:51	59	3/3/2017 23:56	48	5/3/2017 1:01	56	6/3/2017 2:06	58
28/2/2017 4:46	57	1/3/2017 5:51	60	2/3/2017 6:56	59	4/3/2017 0:01	62	5/3/2017 1:06	58	6/3/2017 2:11	57
28/2/2017 4:51	58	1/3/2017 5:56	60	2/3/2017 23:01	56	4/3/2017 0:06	62	5/3/2017 1:11	56	6/3/2017 2:16	57
28/2/2017 4:56	58	1/3/2017 6:01	60	2/3/2017 23:06	57	4/3/2017 0:11	62	5/3/2017 1:16	55	6/3/2017 2:21	56
28/2/2017 5:01	57	1/3/2017 6:06	61	2/3/2017 23:11	64	4/3/2017 0:16	62	5/3/2017 1:21	54	6/3/2017 2:26	56
28/2/2017 5:06	57	1/3/2017 6:11	61	2/3/2017 23:16	56	4/3/2017 0:21	52	5/3/2017 1:26	57	6/3/2017 2:31	56
28/2/2017 5:11	57	1/3/2017 6:16	62	2/3/2017 23:21	48	4/3/2017 0:26	54	5/3/2017 1:31	57	6/3/2017 2:36	56
28/2/2017 5:16	58	1/3/2017 6:21	61	2/3/2017 23:26	57	4/3/2017 0:31	62	5/3/2017 1:36	57	6/3/2017 2:41	57
28/2/2017 5:21	59	1/3/2017 6:26	55	2/3/2017 23:31	45	4/3/2017 0:36	61	5/3/2017 1:41	54	6/3/2017 2:46	56
28/2/2017 5:26	59	1/3/2017 6:31	50	2/3/2017 23:36	49	4/3/2017 0:41	61	5/3/2017 1:46	51	6/3/2017 2:51	55
28/2/2017 5:31	59	1/3/2017 6:36	55	2/3/2017 23:41	52	4/3/2017 0:46	61	5/3/2017 1:51	49	6/3/2017 2:56	57
28/2/2017 5:36	59	1/3/2017 6:41	58	2/3/2017 23:46	62	4/3/2017 0:51	47	5/3/2017 1:56	51	6/3/2017 3:01	58
28/2/2017 5:41	59	1/3/2017 6:46	58	2/3/2017 23:51	61	4/3/2017 0:56	61	5/3/2017 2:01	53	6/3/2017 3:06	55
28/2/2017 5:46	59	1/3/2017 6:51	55	2/3/2017 23:56	61	4/3/2017 1:01	61	5/3/2017 2:06	50	6/3/2017 3:11	57
28/2/2017 5:51	60	1/3/2017 6:56	56	3/3/2017 0:01	40	4/3/2017 1:06	62	5/3/2017 2:11	51	6/3/2017 3:16	56
28/2/2017 5:56	60	1/3/2017 23:01	48	3/3/2017 0:06	62	4/3/2017 1:11	62	5/3/2017 2:16	52	6/3/2017 3:21	57
28/2/2017 6:01	60	1/3/2017 23:06	57	3/3/2017 0:11	61	4/3/2017 1:16	61	5/3/2017 2:21	59	6/3/2017 3:26	56
28/2/2017 6:06	60	1/3/2017 23:11	55	3/3/2017 0:16	61	4/3/2017 1:21	60	5/3/2017 2:26	49	6/3/2017 3:31	58
28/2/2017 6:11	61	1/3/2017 23:16	55	3/3/2017 0:21	54	4/3/2017 1:26	61	5/3/2017 2:31	52	6/3/2017 3:36	56
28/2/2017 6:16	60	1/3/2017 23:21	54	3/3/2017 0:26	61	4/3/2017 1:31	60	5/3/2017 2:36	53	6/3/2017 3:41	57
28/2/2017 6:21	61	1/3/2017 23:26	49	3/3/2017 0:31	54	4/3/2017 1:36	61	5/3/2017 2:41	51	6/3/2017 3:46	56
28/2/2017 6:26	61	1/3/2017 23:31	62	3/3/2017 0:36	60	4/3/2017 1:41	61	5/3/2017 2:46	47	6/3/2017 3:51	57
28/2/2017 6:31	54	1/3/2017 23:36	36	3/3/2017 0:41	61	4/3/2017 1:46	61	5/3/2017 2:51	62	6/3/2017 3:56	56
28/2/2017 6:36	55	1/3/2017 23:41	46	3/3/2017 0:46	60	4/3/2017 1:51	60	5/3/2017 2:56	62	6/3/2017 4:01	56
28/2/2017 6:41	56	1/3/2017 23:46	51	3/3/2017 0:51	61	4/3/2017 1:56	60	5/3/2017 3:01	62	6/3/2017 4:06	57
28/2/2017 6:46	60	1/3/2017 23:51	40	3/3/2017 0:56	52	4/3/2017 2:01	60	5/3/2017 3:06	50	6/3/2017 4:11	57
28/2/2017 6:51	58	1/3/2017 23:56	50	3/3/2017 1:01	61	4/3/2017 2:06	60	5/3/2017 3:11	61	6/3/2017 4:16	56
28/2/2017 6:56	60	2/3/2017 0:01	62	3/3/2017 1:06	61	4/3/2017 2:11	60	5/3/2017 3:16	62	6/3/2017 4:21	56
28/2/2017 23:01	54	2/3/2017 0:06	61	3/3/2017 1:11	60	4/3/2017 2:16	59	5/3/2017 3:21	61	6/3/2017 4:26	57
28/2/2017 23:06	57	2/3/2017 0:11	61	3/3/2017 1:16	60	4/3/2017 2:21	60	5/3/2017 3:26	62	6/3/2017 4:31	57
28/2/2017 23:11	55	2/3/2017 0:16	61	3/3/2017 1:21	60	4/3/2017 2:26	60	5/3/2017 3:31	62	6/3/2017 4:36	56
28/2/2017 23:16	55	2/3/2017 0:21	62	3/3/2017 1:26	60	4/3/2017 2:31	60	5/3/2017 3:36	62	6/3/2017 4:41	56
28/2/2017 23:21	47	2/3/2017 0:26	61	3/3/2017 1:31	60	4/3/2017 2:36	59	5/3/2017 3:41	49	6/3/2017 4:46	

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
6/3/2017 23:26	46	8/3/2017 0:31	60	9/3/2017 1:36	56	10/3/2017 2:41	62	11/3/2017 3:46	57	12/3/2017 4:51	58
6/3/2017 23:31	62	8/3/2017 0:36	61	9/3/2017 1:41	58	10/3/2017 2:46	62	11/3/2017 3:51	58	12/3/2017 4:56	58
6/3/2017 23:36	61	8/3/2017 0:41	59	9/3/2017 1:46	55	10/3/2017 2:51	61	11/3/2017 3:56	58	12/3/2017 5:01	57
6/3/2017 23:41	61	8/3/2017 0:46	60	9/3/2017 1:51	53	10/3/2017 2:56	62	11/3/2017 4:01	57	12/3/2017 5:06	58
6/3/2017 23:46	61	8/3/2017 0:51	59	9/3/2017 1:56	53	10/3/2017 3:01	61	11/3/2017 4:06	58	12/3/2017 5:11	58
6/3/2017 23:51	61	8/3/2017 0:56	61	9/3/2017 2:01	49	10/3/2017 3:06	61	11/3/2017 4:11	57	12/3/2017 5:16	58
6/3/2017 23:56	61	8/3/2017 1:01	60	9/3/2017 2:06	47	10/3/2017 3:11	61	11/3/2017 4:16	59	12/3/2017 5:21	58
7/3/2017 0:01	61	8/3/2017 1:06	60	9/3/2017 2:11	62	10/3/2017 3:16	61	11/3/2017 4:21	59	12/3/2017 5:26	58
7/3/2017 0:06	61	8/3/2017 1:11	59	9/3/2017 2:16	45	10/3/2017 3:21	61	11/3/2017 4:26	58	12/3/2017 5:31	59
7/3/2017 0:11	62	8/3/2017 1:16	59	9/3/2017 2:21	62	10/3/2017 3:26	61	11/3/2017 4:31	58	12/3/2017 5:36	59
7/3/2017 0:16	61	8/3/2017 1:21	60	9/3/2017 2:26	54	10/3/2017 3:31	61	11/3/2017 4:36	57	12/3/2017 5:41	59
7/3/2017 0:21	61	8/3/2017 1:26	59	9/3/2017 2:31	52	10/3/2017 3:36	62	11/3/2017 4:41	59	12/3/2017 5:46	60
7/3/2017 0:26	60	8/3/2017 1:31	59	9/3/2017 2:36	59	10/3/2017 3:41	61	11/3/2017 4:46	57	12/3/2017 5:51	60
7/3/2017 0:31	60	8/3/2017 1:36	61	9/3/2017 2:41	55	10/3/2017 3:46	62	11/3/2017 4:51	58	12/3/2017 5:56	60
7/3/2017 0:36	61	8/3/2017 1:41	58	9/3/2017 2:46	61	10/3/2017 3:51	61	11/3/2017 4:56	58	12/3/2017 6:01	60
7/3/2017 0:41	61	8/3/2017 1:46	58	9/3/2017 2:51	62	10/3/2017 3:56	56	11/3/2017 5:01	59	12/3/2017 6:06	60
7/3/2017 0:46	60	8/3/2017 1:51	59	9/3/2017 2:56	62	10/3/2017 4:01	61	11/3/2017 5:06	59	12/3/2017 6:11	61
7/3/2017 0:51	60	8/3/2017 1:56	58	9/3/2017 3:01	61	10/3/2017 4:06	61	11/3/2017 5:11	59	12/3/2017 6:16	60
7/3/2017 0:56	61	8/3/2017 2:01	59	9/3/2017 3:06	61	10/3/2017 4:11	61	11/3/2017 5:16	58	12/3/2017 6:21	61
7/3/2017 1:01	60	8/3/2017 2:06	58	9/3/2017 3:11	62	10/3/2017 4:16	61	11/3/2017 5:21	58	12/3/2017 6:26	62
7/3/2017 1:06	60	8/3/2017 2:11	58	9/3/2017 3:16	62	10/3/2017 4:21	61	11/3/2017 5:26	59	12/3/2017 6:31	62
7/3/2017 1:11	60	8/3/2017 2:16	59	9/3/2017 3:21	61	10/3/2017 4:26	61	11/3/2017 5:31	59	12/3/2017 6:36	62
7/3/2017 1:16	60	8/3/2017 2:21	59	9/3/2017 3:26	61	10/3/2017 4:31	61	11/3/2017 5:36	59	12/3/2017 6:41	48
7/3/2017 1:21	60	8/3/2017 2:26	57	9/3/2017 3:31	62	10/3/2017 4:36	61	11/3/2017 5:41	58	12/3/2017 6:46	53
7/3/2017 1:26	59	8/3/2017 2:31	57	9/3/2017 3:36	62	10/3/2017 4:41	61	11/3/2017 5:46	60	12/3/2017 6:51	53
7/3/2017 1:31	59	8/3/2017 2:36	58	9/3/2017 3:41	61	10/3/2017 4:46	61	11/3/2017 5:51	60	12/3/2017 6:56	54
7/3/2017 1:36	60	8/3/2017 2:41	58	9/3/2017 3:46	61	10/3/2017 4:51	61	11/3/2017 5:56	59	12/3/2017 7:01	62
7/3/2017 1:41	59	8/3/2017 2:46	58	9/3/2017 3:51	61	10/3/2017 4:56	61	11/3/2017 6:01	59	12/3/2017 7:06	52
7/3/2017 1:46	58	8/3/2017 2:51	58	9/3/2017 3:56	61	10/3/2017 5:01	61	11/3/2017 6:06	60	12/3/2017 7:11	48
7/3/2017 1:51	58	8/3/2017 2:56	56	9/3/2017 4:01	61	10/3/2017 5:06	61	11/3/2017 6:11	60	12/3/2017 7:16	61
7/3/2017 1:56	59	8/3/2017 3:01	57	9/3/2017 4:06	61	10/3/2017 5:11	61	11/3/2017 6:16	59	12/3/2017 7:21	62
7/3/2017 2:01	58	8/3/2017 3:06	57	9/3/2017 4:11	61	10/3/2017 5:16	61	11/3/2017 6:21	60	12/3/2017 7:26	61
7/3/2017 2:06	58	8/3/2017 3:11	57	9/3/2017 4:16	62	10/3/2017 5:21	61	11/3/2017 6:26	61	12/3/2017 7:31	61
7/3/2017 2:11	59	8/3/2017 3:16	56	9/3/2017 4:21	61	10/3/2017 5:26	46	11/3/2017 6:31	61	12/3/2017 7:36	61
7/3/2017 2:16	57	8/3/2017 3:21	56	9/3/2017 4:26	62	10/3/2017 5:31	48	11/3/2017 6:36	45	12/3/2017 7:41	50
7/3/2017 2:21	58	8/3/2017 3:26	56	9/3/2017 4:31	61	10/3/2017 5:36	48	11/3/2017 6:41	46	12/3/2017 7:46	62
7/3/2017 2:26	58	8/3/2017 3:31	57	9/3/2017 4:36	61	10/3/2017 5:41	51	11/3/2017 6:46	42	12/3/2017 7:51	61
7/3/2017 2:31	58	8/3/2017 3:36	57	9/3/2017 4:41	62	10/3/2017 5:46	48	11/3/2017 6:51	51	12/3/2017 7:56	46
7/3/2017 2:36	58	8/3/2017 3:41	56	9/3/2017 4:46	61	10/3/2017 5:51	53	11/3/2017 6:56	62	13/3/2017 0:01	61
7/3/2017 2:41	57	8/3/2017 3:46	58	9/3/2017 4:51	61	10/3/2017 5:56	46	11/3/2017 7:01	60	13/3/2017 0:06	60
7/3/2017 2:46	58	8/3/2017 3:51	57	9/3/2017 4:56	62	10/3/2017 6:01	54	11/3/2017 7:06	57	13/3/2017 0:11	61
7/3/2017 2:51	57	8/3/2017 3:56	57	9/3/2017 5:01	61	10/3/2017 6:06	55	11/3/2017 7:11	55	13/3/2017 0:16	60
7/3/2017 2:56	57	8/3/2017 4:01	57	9/3/2017 5:06	62	10/3/2017 6:11	53	11/3/2017 7:16	51	13/3/2017 0:21	60
7/3/2017 3:01	57	8/3/2017 4:06	57	9/3/2017 5:11	62	10/3/2017 6:16	57	11/3/2017 7:21	53	13/3/2017 0:26	60
7/3/2017 3:06	56	8/3/2017 4:11	57	9/3/2017 5:16	62	10/3/2017 6:21	56	11/3/2017 7:26	47	13/3/2017 0:31	60
7/3/2017 3:11	57	8/3/2017 4:16	57	9/3/2017 5:21	62	10/3/2017 6:26	60	11/3/2017 7:31	36	13/3/2017 0:36	61
7/3/2017 3:16	57	8/3/2017 4:21	57	9/3/2017 5:26	62	10/3/2017 6:31	59	11/3/2017 7:36	61	13/3/2017 0:41	60
7/3/2017 3:21	57	8/3/2017 4:26	56	9/3/2017 5:31	52	10/3/2017 6:36	60	11/3/2017 7:41	54	13/3/2017 0:46	60
7/3/2017 3:26	56	8/3/2017 4:31	58	9/3/2017 5:36	61	10/3/2017 6:41	61	11/3/2017 7:46	62	13/3/2017 0:51	61
7/3/2017 3:31	58	8/3/2017 4:36	57	9/3/2017 5:41	62	10/3/2017 6:46	61	11/3/2017 7:51	52	13/3/2017 0:56	59
7/3/2017 3:36	58	8/3/2017 4:41	57	9/3/2017 5:46	62	10/3/2017 6:51	62	11/3/2017 7:56	62	13/3/2017 1:01	60
7/3/2017 3:41	58	8/3/2017 4:46	57	9/3/2017 5:51	54	10/3/2017 6:56	62	12/3/2017 0:01	62	13/3/2017 1:06	60
7/3/2017 3:46	58	8/3/2017 4:51	58	9/3/2017 5:56	55	10/3/2017 7:01	56	12/3/2017 0:06	61	13/3/2017 1:11	58
7/3/2017 3:51	57	8/3/2017 4:56	57	9/3/2017 6:01	54	10/3/2017 7:06	57	12/3/2017 0:11	61	13/3/2017 1:16	59
7/3/2017 3:56	57	8/3/2017 5:01	57	9/3/2017 6:06	55	10/3/2017 7:11	55	12/3/2017 0:16	61	13/3/2017 1:21	59
7/3/2017 4:01	56	8/3/2017 5:06	57	9/3/2017 6:11	55	10/3/2017 7:16	55	12/3/2017 0:21	61	13/3/2017 1:26	59
7/3/2017 4:06	58	8/3/2017 5:11	57	9/3/2017 6:16	58	10/3/2017 7:21	55	12/3/2017 0:26	61	13/3/2017 1:31	59
7/3/2017 4:11	56	8/3/2017 5:16	57	9/3/2017 6:21	58	10/3/2017 7:26	53	12/3/2017 0:31	61	13/3/2017 1:36	58
7/3/2017 4:16	57	8/3/2017 5:21	57	9/3/2017 6:26	61	10/3/2017 7:31	55	12/3/2017 0:36	61	13/3/2017 1:41	58
7/3/2017 4:21	58	8/3/2017 5:26	59	9/3/2017 6:31	60	10/3/2017 7:36	60	12/3/2017 0:41	61	13/3/2017 1:46	58
7/3/2017 4:26	57	8/3/2017 5:31	59	9/3/2017 6:36	61	10/3/2017 7:41	55	12/3/2017 0:46	61	13/3/2017 1:51	59
7/3/2017 4:31	57	8/3/2017 5:36	59	9/3/2017 6:41	61	10/3/2017 7:46	53	12/3/2017 0:51	61	13/3/2017 1:56	60
7/3/2017 4:36	57	8/3/2017 5:41	58	9/3/2017 6:46	61	10/3/2017 7:51	62	12/3/2017 0:56	61	13/3/2017 2:01	57
7/3/2017 4:41	57	8/3/2017 5:46	59	9/3/2017 6:51	61	10/3/2017 7:56	62	12/3/2017 1:01	61	13/3/2017 2:06	57
7/3/2017 4:46	58	8/3/2017 5:51	60	9/3/2017 6:56	62	11/3/2017 0:01	54	12/3/2017 1:06	61	13/3/2017 2:11	58
7/3/2017 4:51	58	8/3/2017 5:56	60	9/3/2017 7:01	60	11/3/2017 0:06	62	12/3/2017 1:11	61	13/3/2017 2:16	57
7/3/2017 4:56	57	8/3/2017 6:01	61	9/3/2017 7:06	60	11/3/2017 0:11	61	12/3/2017 1:16	61	13/3/2017 2:21	58
7/3/2017 5:01	57	8/3/2017 6:06	60	9/3/2017 7:11	60	11/3/2017 0:16	61	12/3/2017 1:21	61	13/3/2017 2:26	57
7/3/2017 5:06	57	8/3/2017 6:11	61	9/3/2017 7:16	60	11/3/2017 0:21	61	12/3/2017 1:26	61	13/3/2017 2:31	58
7/3/2017 5:11	58	8/3/2017 6:16	61	9/3/2017 7:21	61	11/3/2017 0:26	57	12/3/2017 1:31	60	13/3/2017 2:36	57
7/3/2017 5:16	58	8/3/2017 6:21	61	9/3/2017 7:26	60	11/3/2017 0:31	61	12/3/2017 1:36	60	13/3/2017 2:41	57
7/3/2017 5:21	58	8/3/2017 6:26	62	9/3/2017 7:31	60	11/3/2017 0:36	61	12/3/2017 1:41	61	13/3/2017 2:46	58
7/3/2017 5:26	59	8/3/2017 6:31	54	9/3/2017 7:36	58	11/3/2017 0:41	61	12/3/2017 1:46	61	13/3/2017 2:51	57
7/3/2017 5:31	58	8/3/2017 6:36	53	9/3/2017 7:41	59	11/3/2017 0:46	61	12/3/2017 1:51	61	13/3/2017 2:56	57
7/3/2017 5:36	59	8/3/2017 6:41	57	9/3/2017 7:46	58	11/3/2017 0:51	60	12/3/2017 1:56	61	13/3/2017 3:01	56
7/3/2017 5:41	59	8/3/2017 6:46	57	9/3/2017 7:51	57	11/3/2017 0:56	61	12/3/2017 2:01	60	13/3/2017 3:06	58
7/3/2017 5:46	59	8/3/2017 6:51	59	9/3/2017 7:56	58	11/3/2017 1:01	61	12/3/2017 2:06	61	13/3/2017 3:11	56
7/3/2017 5:51	59	8/3/2017 6:56	59								

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
13/3/2017 5:56	60	14/3/2017 23:01	56	16/3/2017 0:06	62	17/3/2017 1:11	61	18/3/2017 2:16	55	19/3/2017 3:21	59
13/3/2017 6:01	60	14/3/2017 23:06	50	16/3/2017 0:11	61	17/3/2017 1:16	60	18/3/2017 2:21	58	19/3/2017 3:26	60
13/3/2017 6:06	60	14/3/2017 23:11	55	16/3/2017 0:16	62	17/3/2017 1:21	60	18/3/2017 2:26	57	19/3/2017 3:31	59
13/3/2017 6:11	60	14/3/2017 23:16	56	16/3/2017 0:21	61	17/3/2017 1:26	59	18/3/2017 2:31	57	19/3/2017 3:36	58
13/3/2017 6:16	61	14/3/2017 23:21	56	16/3/2017 0:26	53	17/3/2017 1:31	58	18/3/2017 2:36	55	19/3/2017 3:41	59
13/3/2017 6:21	61	14/3/2017 23:26	57	16/3/2017 0:31	61	17/3/2017 1:36	60	18/3/2017 2:41	55	19/3/2017 3:46	58
13/3/2017 6:26	47	14/3/2017 23:31	55	16/3/2017 0:36	61	17/3/2017 1:41	59	18/3/2017 2:46	58	19/3/2017 3:51	58
13/3/2017 6:31	45	14/3/2017 23:36	54	16/3/2017 0:41	61	17/3/2017 1:46	59	18/3/2017 2:51	57	19/3/2017 3:56	57
13/3/2017 6:36	54	14/3/2017 23:41	52	16/3/2017 0:46	61	17/3/2017 1:51	59	18/3/2017 2:56	55	19/3/2017 4:01	58
13/3/2017 6:41	56	14/3/2017 23:46	62	16/3/2017 0:51	52	17/3/2017 1:56	59	18/3/2017 3:01	55	19/3/2017 4:06	59
13/3/2017 6:46	58	14/3/2017 23:51	62	16/3/2017 0:56	61	17/3/2017 2:01	59	18/3/2017 3:06	55	19/3/2017 4:11	58
13/3/2017 6:51	57	14/3/2017 23:56	61	16/3/2017 1:01	60	17/3/2017 2:06	59	18/3/2017 3:11	56	19/3/2017 4:16	58
13/3/2017 6:56	56	15/3/2017 0:01	52	16/3/2017 1:06	61	17/3/2017 2:11	58	18/3/2017 3:16	55	19/3/2017 4:21	58
13/3/2017 23:01	55	15/3/2017 0:06	61	16/3/2017 1:11	61	17/3/2017 2:16	58	18/3/2017 3:21	53	19/3/2017 4:26	60
13/3/2017 23:06	53	15/3/2017 0:11	61	16/3/2017 1:16	60	17/3/2017 2:21	60	18/3/2017 3:26	52	19/3/2017 4:31	58
13/3/2017 23:11	55	15/3/2017 0:16	62	16/3/2017 1:21	60	17/3/2017 2:26	59	18/3/2017 3:31	55	19/3/2017 4:36	57
13/3/2017 23:16	54	15/3/2017 0:21	50	16/3/2017 1:26	60	17/3/2017 2:31	58	18/3/2017 3:36	55	19/3/2017 4:41	58
13/3/2017 23:21	51	15/3/2017 0:26	62	16/3/2017 1:31	60	17/3/2017 2:36	59	18/3/2017 3:41	53	19/3/2017 4:46	58
13/3/2017 23:26	62	15/3/2017 0:31	61	16/3/2017 1:36	60	17/3/2017 2:41	58	18/3/2017 3:46	54	19/3/2017 4:51	58
13/3/2017 23:31	61	15/3/2017 0:36	61	16/3/2017 1:41	61	17/3/2017 2:46	59	18/3/2017 3:51	54	19/3/2017 4:56	59
13/3/2017 23:36	45	15/3/2017 0:41	60	16/3/2017 1:46	59	17/3/2017 2:51	59	18/3/2017 3:56	55	19/3/2017 5:01	58
13/3/2017 23:41	46	15/3/2017 0:46	60	16/3/2017 1:51	59	17/3/2017 2:56	59	18/3/2017 4:01	45	19/3/2017 5:06	58
13/3/2017 23:46	61	15/3/2017 0:51	60	16/3/2017 1:56	59	17/3/2017 3:01	58	18/3/2017 4:06	55	19/3/2017 5:11	58
13/3/2017 23:51	58	15/3/2017 0:56	60	16/3/2017 2:01	60	17/3/2017 3:06	58	18/3/2017 4:11	54	19/3/2017 5:16	58
13/3/2017 23:56	61	15/3/2017 1:01	61	16/3/2017 2:06	58	17/3/2017 3:11	57	18/3/2017 4:16	52	19/3/2017 5:21	59
14/3/2017 0:01	61	15/3/2017 1:06	59	16/3/2017 2:11	59	17/3/2017 3:16	57	18/3/2017 4:21	56	19/3/2017 5:26	58
14/3/2017 0:06	61	15/3/2017 1:11	60	16/3/2017 2:16	58	17/3/2017 3:21	58	18/3/2017 4:26	55	19/3/2017 5:31	59
14/3/2017 0:11	60	15/3/2017 1:16	60	16/3/2017 2:21	58	17/3/2017 3:26	57	18/3/2017 4:31	52	19/3/2017 5:36	59
14/3/2017 0:16	61	15/3/2017 1:21	60	16/3/2017 2:26	58	17/3/2017 3:31	57	18/3/2017 4:36	52	19/3/2017 5:41	60
14/3/2017 0:21	61	15/3/2017 1:26	59	16/3/2017 2:31	59	17/3/2017 3:36	57	18/3/2017 4:41	55	19/3/2017 5:46	60
14/3/2017 0:26	61	15/3/2017 1:31	62	16/3/2017 2:36	59	17/3/2017 3:41	57	18/3/2017 4:46	53	19/3/2017 5:51	60
14/3/2017 0:31	60	15/3/2017 1:36	59	16/3/2017 2:41	58	17/3/2017 3:46	57	18/3/2017 4:51	53	19/3/2017 5:56	60
14/3/2017 0:36	60	15/3/2017 1:41	59	16/3/2017 2:46	59	17/3/2017 3:51	60	18/3/2017 4:56	53	19/3/2017 6:01	59
14/3/2017 0:41	62	15/3/2017 1:46	60	16/3/2017 2:51	57	17/3/2017 3:56	57	18/3/2017 5:01	52	19/3/2017 6:06	60
14/3/2017 0:46	61	15/3/2017 1:51	59	16/3/2017 2:56	59	17/3/2017 4:01	57	18/3/2017 5:06	53	19/3/2017 6:11	59
14/3/2017 0:51	60	15/3/2017 1:56	60	16/3/2017 3:01	58	17/3/2017 4:06	58	18/3/2017 5:11	48	19/3/2017 6:16	60
14/3/2017 0:56	60	15/3/2017 2:01	58	16/3/2017 3:06	59	17/3/2017 4:11	57	18/3/2017 5:16	54	19/3/2017 6:21	60
14/3/2017 1:01	61	15/3/2017 2:06	58	16/3/2017 3:11	58	17/3/2017 4:16	57	18/3/2017 5:21	54	19/3/2017 6:26	61
14/3/2017 1:06	60	15/3/2017 2:11	59	16/3/2017 3:16	58	17/3/2017 4:21	57	18/3/2017 5:26	55	19/3/2017 6:31	61
14/3/2017 1:11	60	15/3/2017 2:16	59	16/3/2017 3:21	58	17/3/2017 4:26	57	18/3/2017 5:31	55	19/3/2017 6:36	61
14/3/2017 1:16	59	15/3/2017 2:21	60	16/3/2017 3:26	59	17/3/2017 4:31	56	18/3/2017 5:36	55	19/3/2017 6:41	62
14/3/2017 1:21	47	15/3/2017 2:26	58	16/3/2017 3:31	58	17/3/2017 4:36	57	18/3/2017 5:41	54	19/3/2017 6:46	61
14/3/2017 1:26	59	15/3/2017 2:31	59	16/3/2017 3:36	58	17/3/2017 4:41	57	18/3/2017 5:46	54	19/3/2017 6:51	61
14/3/2017 1:31	59	15/3/2017 2:36	59	16/3/2017 3:41	57	17/3/2017 4:46	57	18/3/2017 5:51	55	19/3/2017 6:56	61
14/3/2017 1:36	60	15/3/2017 2:41	57	16/3/2017 3:46	59	17/3/2017 4:51	58	18/3/2017 5:56	54	19/3/2017 7:01	54
14/3/2017 1:41	60	15/3/2017 2:46	58	16/3/2017 3:51	57	17/3/2017 4:56	58	18/3/2017 6:01	55	19/3/2017 7:06	55
14/3/2017 1:46	58	15/3/2017 2:51	58	16/3/2017 3:56	57	17/3/2017 5:01	57	18/3/2017 6:06	55	19/3/2017 7:11	49
14/3/2017 1:51	59	15/3/2017 2:56	59	16/3/2017 4:01	57	17/3/2017 5:06	58	18/3/2017 6:11	58	19/3/2017 7:16	57
14/3/2017 1:56	59	15/3/2017 3:01	57	16/3/2017 4:06	57	17/3/2017 5:11	56	18/3/2017 6:16	58	19/3/2017 7:21	62
14/3/2017 2:01	58	15/3/2017 3:06	58	16/3/2017 4:11	57	17/3/2017 5:16	59	18/3/2017 6:21	57	19/3/2017 7:26	54
14/3/2017 2:06	58	15/3/2017 3:11	58	16/3/2017 4:16	58	17/3/2017 5:21	59	18/3/2017 6:26	58	19/3/2017 7:31	48
14/3/2017 2:11	58	15/3/2017 3:16	57	16/3/2017 4:21	58	17/3/2017 5:26	59	18/3/2017 6:31	61	19/3/2017 7:36	62
14/3/2017 2:16	58	15/3/2017 3:21	58	16/3/2017 4:26	58	17/3/2017 5:31	58	18/3/2017 6:36	61	19/3/2017 7:41	52
14/3/2017 2:21	57	15/3/2017 3:26	58	16/3/2017 4:31	58	17/3/2017 5:36	58	18/3/2017 6:41	48	19/3/2017 7:46	53
14/3/2017 2:26	58	15/3/2017 3:31	58	16/3/2017 4:36	58	17/3/2017 5:41	60	18/3/2017 6:46	47	19/3/2017 7:51	49
14/3/2017 2:31	57	15/3/2017 3:36	58	16/3/2017 4:41	56	17/3/2017 5:46	59	18/3/2017 6:51	52	19/3/2017 7:56	61
14/3/2017 2:36	58	15/3/2017 3:41	58	16/3/2017 4:46	58	17/3/2017 5:51	60	18/3/2017 6:56	62	20/3/2017 0:01	61
14/3/2017 2:41	58	15/3/2017 3:46	59	16/3/2017 4:51	57	17/3/2017 5:56	60	18/3/2017 7:01	57	20/3/2017 0:06	61
14/3/2017 2:46	58	15/3/2017 3:51	57	16/3/2017 4:56	58	17/3/2017 6:01	60	18/3/2017 7:06	58	20/3/2017 0:11	61
14/3/2017 2:51	58	15/3/2017 3:56	57	16/3/2017 5:01	58	17/3/2017 6:06	61	18/3/2017 7:11	56	20/3/2017 0:16	61
14/3/2017 2:56	57	15/3/2017 4:01	57	16/3/2017 5:06	58	17/3/2017 6:11	61	18/3/2017 7:16	55	20/3/2017 0:21	61
14/3/2017 3:01	59	15/3/2017 4:06	57	16/3/2017 5:11	58	17/3/2017 6:16	62	18/3/2017 7:21	55	20/3/2017 0:26	61
14/3/2017 3:06	57	15/3/2017 4:11	59	16/3/2017 5:16	59	17/3/2017 6:21	61	18/3/2017 7:26	55	20/3/2017 0:31	61
14/3/2017 3:11	57	15/3/2017 4:16	57	16/3/2017 5:21	58	17/3/2017 6:26	48	18/3/2017 7:31	58	20/3/2017 0:36	60
14/3/2017 3:16	57	15/3/2017 4:21	57	16/3/2017 5:26	58	17/3/2017 6:31	52	18/3/2017 7:36	57	20/3/2017 0:41	61
14/3/2017 3:21	57	15/3/2017 4:26	58	16/3/2017 5:31	59	17/3/2017 6:36	56	18/3/2017 7:41	53	20/3/2017 0:46	60
14/3/2017 3:26	57	15/3/2017 4:31	58	16/3/2017 5:36	59	17/3/2017 6:41	57	18/3/2017 7:46	51	20/3/2017 0:51	59
14/3/2017 3:31	58	15/3/2017 4:36	58	16/3/2017 5:41	59	17/3/2017 6:46	58	18/3/2017 7:51	62	20/3/2017 0:56	61
14/3/2017 3:36	57	15/3/2017 4:41	57	16/3/2017 5:46	60	17/3/2017 6:51	58	18/3/2017 7:56	63	20/3/2017 1:01	60
14/3/2017 3:41	57	15/3/2017 4:46	57	16/3/2017 5:51	60	17/3/2017 6:56	60	19/3/2017 0:01	50	20/3/2017 1:06	60
14/3/2017 3:46	57	15/3/2017 4:51	58	16/3/2017 5:56	60	17/3/2017 7:01	60	19/3/2017 0:06	62	20/3/2017 1:11	60
14/3/2017 3:51	57	15/3/2017 4:56	58	16/3/2017 6:01	60	17/3/2017 7:06	62	19/3/2017 0:11	61	20/3/2017 1:16	60
14/3/2017 3:56	57	15/3/2017 5:01	57	16/3/2017 6:06	61	17/3/2017 7:11	62	19/3/2017 0:16	49	20/3/2017 1:21	60
14/3/2017 4:01	57	15/3/2017 5:06	58	16/3/2017 6:11	61	17/3/2017 7:16	63	19/3/2017 0:21	62	20/3/2017 1:26	59
14/3/2017 4:06	58	15/3/2017 5:11	58	16/3/2017 6:16	61	17/3/2017 7:21	61	19/3/2017 0:26	62	20/3/2017 1:31	60
14/3/2017 4:11	57	15/3/2017 5:16	57	16/3/2017 6:21	62	17/3/2017 7:26	62	19/3/2017 0:31			

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
20/3/2017 4:26	58	21/3/2017 5:31	58	22/3/2017 6:36	57	23/3/2017 23:41	54	25/3/2017 0:46	61	26/3/2017 1:51	61
20/3/2017 4:31	57	21/3/2017 5:36	59	22/3/2017 6:41	58	23/3/2017 23:46	54	25/3/2017 0:51	61	26/3/2017 1:56	61
20/3/2017 4:36	57	21/3/2017 5:41	59	22/3/2017 6:46	57	23/3/2017 23:51	46	25/3/2017 0:56	61	26/3/2017 2:01	60
20/3/2017 4:41	58	21/3/2017 5:46	60	22/3/2017 6:51	57	23/3/2017 23:56	52	25/3/2017 1:01	61	26/3/2017 2:06	60
20/3/2017 4:46	59	21/3/2017 5:51	60	22/3/2017 6:56	57	24/3/2017 0:01	62	25/3/2017 1:06	61	26/3/2017 2:11	60
20/3/2017 4:51	56	21/3/2017 5:56	59	22/3/2017 23:01	50	24/3/2017 0:06	61	25/3/2017 1:11	61	26/3/2017 2:16	59
20/3/2017 4:56	58	21/3/2017 6:01	60	22/3/2017 23:06	49	24/3/2017 0:11	61	25/3/2017 1:16	39	26/3/2017 2:21	60
20/3/2017 5:01	58	21/3/2017 6:06	60	22/3/2017 23:11	54	24/3/2017 0:16	61	25/3/2017 1:21	61	26/3/2017 2:26	59
20/3/2017 5:06	58	21/3/2017 6:11	61	22/3/2017 23:16	52	24/3/2017 0:21	61	25/3/2017 1:26	61	26/3/2017 2:31	59
20/3/2017 5:11	58	21/3/2017 6:16	61	22/3/2017 23:21	55	24/3/2017 0:26	62	25/3/2017 1:31	61	26/3/2017 2:36	60
20/3/2017 5:16	58	21/3/2017 6:21	62	22/3/2017 23:26	55	24/3/2017 0:31	62	25/3/2017 1:36	61	26/3/2017 2:41	59
20/3/2017 5:21	59	21/3/2017 6:26	57	22/3/2017 23:31	52	24/3/2017 0:36	61	25/3/2017 1:41	61	26/3/2017 2:46	60
20/3/2017 5:26	59	21/3/2017 6:31	53	22/3/2017 23:36	55	24/3/2017 0:41	61	25/3/2017 1:46	61	26/3/2017 2:51	60
20/3/2017 5:31	59	21/3/2017 6:36	56	22/3/2017 23:41	48	24/3/2017 0:46	61	25/3/2017 1:51	61	26/3/2017 2:56	60
20/3/2017 5:36	60	21/3/2017 6:41	60	22/3/2017 23:46	53	24/3/2017 0:51	61	25/3/2017 1:56	61	26/3/2017 3:01	59
20/3/2017 5:41	60	21/3/2017 6:46	58	22/3/2017 23:51	47	24/3/2017 0:56	61	25/3/2017 2:01	60	26/3/2017 3:06	59
20/3/2017 5:46	60	21/3/2017 6:51	60	22/3/2017 23:56	62	24/3/2017 1:01	60	25/3/2017 2:06	60	26/3/2017 3:11	59
20/3/2017 5:51	61	21/3/2017 6:56	55	23/3/2017 0:01	48	24/3/2017 1:06	61	25/3/2017 2:11	60	26/3/2017 3:16	60
20/3/2017 5:56	60	21/3/2017 23:01	44	23/3/2017 0:06	61	24/3/2017 1:11	60	25/3/2017 2:16	60	26/3/2017 3:21	59
20/3/2017 6:01	60	21/3/2017 23:06	55	23/3/2017 0:11	61	24/3/2017 1:16	61	25/3/2017 2:21	60	26/3/2017 3:26	58
20/3/2017 6:06	61	21/3/2017 23:11	56	23/3/2017 0:16	61	24/3/2017 1:21	60	25/3/2017 2:26	60	26/3/2017 3:31	59
20/3/2017 6:11	62	21/3/2017 23:16	57	23/3/2017 0:21	62	24/3/2017 1:26	60	25/3/2017 2:31	60	26/3/2017 3:36	59
20/3/2017 6:16	53	21/3/2017 23:21	53	23/3/2017 0:26	61	24/3/2017 1:31	60	25/3/2017 2:36	60	26/3/2017 3:41	60
20/3/2017 6:21	52	21/3/2017 23:26	54	23/3/2017 0:31	62	24/3/2017 1:36	59	25/3/2017 2:41	60	26/3/2017 3:46	58
20/3/2017 6:26	57	21/3/2017 23:31	56	23/3/2017 0:36	62	24/3/2017 1:41	59	25/3/2017 2:46	60	26/3/2017 3:51	59
20/3/2017 6:31	57	21/3/2017 23:36	62	23/3/2017 0:41	62	24/3/2017 1:46	59	25/3/2017 2:51	61	26/3/2017 3:56	59
20/3/2017 6:36	58	21/3/2017 23:41	53	23/3/2017 0:46	61	24/3/2017 1:51	59	25/3/2017 2:56	60	26/3/2017 4:01	58
20/3/2017 6:41	60	21/3/2017 23:46	55	23/3/2017 0:51	61	24/3/2017 1:56	59	25/3/2017 3:01	59	26/3/2017 4:06	59
20/3/2017 6:46	60	21/3/2017 23:51	54	23/3/2017 0:56	61	24/3/2017 2:01	59	25/3/2017 3:06	60	26/3/2017 4:11	58
20/3/2017 6:51	61	21/3/2017 23:56	62	23/3/2017 1:01	61	24/3/2017 2:06	58	25/3/2017 3:11	60	26/3/2017 4:16	59
20/3/2017 6:56	61	22/3/2017 0:01	62	23/3/2017 1:06	61	24/3/2017 2:11	58	25/3/2017 3:16	60	26/3/2017 4:21	58
20/3/2017 23:01	52	22/3/2017 0:06	62	23/3/2017 1:11	61	24/3/2017 2:16	57	25/3/2017 3:21	59	26/3/2017 4:26	59
20/3/2017 23:06	55	22/3/2017 0:11	61	23/3/2017 1:16	60	24/3/2017 2:21	58	25/3/2017 3:26	59	26/3/2017 4:31	59
20/3/2017 23:11	50	22/3/2017 0:16	61	23/3/2017 1:21	60	24/3/2017 2:26	59	25/3/2017 3:31	58	26/3/2017 4:36	58
20/3/2017 23:16	51	22/3/2017 0:21	61	23/3/2017 1:26	60	24/3/2017 2:31	58	25/3/2017 3:36	59	26/3/2017 4:41	58
20/3/2017 23:21	54	22/3/2017 0:26	62	23/3/2017 1:31	60	24/3/2017 2:36	58	25/3/2017 3:41	60	26/3/2017 4:46	58
20/3/2017 23:26	51	22/3/2017 0:31	61	23/3/2017 1:36	61	24/3/2017 2:41	58	25/3/2017 3:46	59	26/3/2017 4:51	59
20/3/2017 23:31	53	22/3/2017 0:36	61	23/3/2017 1:41	60	24/3/2017 2:46	58	25/3/2017 3:51	59	26/3/2017 4:56	58
20/3/2017 23:36	62	22/3/2017 0:41	60	23/3/2017 1:46	60	24/3/2017 2:51	57	25/3/2017 3:56	58	26/3/2017 5:01	57
20/3/2017 23:41	62	22/3/2017 0:46	61	23/3/2017 1:51	60	24/3/2017 2:56	58	25/3/2017 4:01	59	26/3/2017 5:06	58
20/3/2017 23:46	61	22/3/2017 0:51	61	23/3/2017 1:56	60	24/3/2017 3:01	57	25/3/2017 4:06	59	26/3/2017 5:11	58
20/3/2017 23:51	62	22/3/2017 0:56	60	23/3/2017 2:01	59	24/3/2017 3:06	57	25/3/2017 4:11	60	26/3/2017 5:16	59
20/3/2017 23:56	62	22/3/2017 1:01	60	23/3/2017 2:06	59	24/3/2017 3:11	57	25/3/2017 4:16	60	26/3/2017 5:21	59
21/3/2017 0:01	61	22/3/2017 1:06	61	23/3/2017 2:11	60	24/3/2017 3:16	57	25/3/2017 4:21	59	26/3/2017 5:26	59
21/3/2017 0:06	61	22/3/2017 1:11	60	23/3/2017 2:16	59	24/3/2017 3:21	58	25/3/2017 4:26	59	26/3/2017 5:31	59
21/3/2017 0:11	61	22/3/2017 1:16	62	23/3/2017 2:21	60	24/3/2017 3:26	57	25/3/2017 4:31	59	26/3/2017 5:36	59
21/3/2017 0:16	61	22/3/2017 1:21	60	23/3/2017 2:26	59	24/3/2017 3:31	58	25/3/2017 4:36	58	26/3/2017 5:41	59
21/3/2017 0:21	47	22/3/2017 1:26	60	23/3/2017 2:31	60	24/3/2017 3:36	58	25/3/2017 4:41	58	26/3/2017 5:46	59
21/3/2017 0:26	61	22/3/2017 1:31	60	23/3/2017 2:36	60	24/3/2017 3:41	57	25/3/2017 4:46	57	26/3/2017 5:51	60
21/3/2017 0:31	61	22/3/2017 1:36	60	23/3/2017 2:41	60	24/3/2017 3:46	57	25/3/2017 4:51	58	26/3/2017 5:56	60
21/3/2017 0:36	60	22/3/2017 1:41	59	23/3/2017 2:46	59	24/3/2017 3:51	58	25/3/2017 4:56	59	26/3/2017 6:01	59
21/3/2017 0:41	61	22/3/2017 1:46	60	23/3/2017 2:51	59	24/3/2017 3:56	58	25/3/2017 5:01	60	26/3/2017 6:06	60
21/3/2017 0:46	61	22/3/2017 1:51	59	23/3/2017 2:56	59	24/3/2017 4:01	58	25/3/2017 5:06	59	26/3/2017 6:11	60
21/3/2017 0:51	60	22/3/2017 1:56	58	23/3/2017 3:01	59	24/3/2017 4:06	57	25/3/2017 5:11	58	26/3/2017 6:16	61
21/3/2017 0:56	60	22/3/2017 2:01	59	23/3/2017 3:06	59	24/3/2017 4:11	58	25/3/2017 5:16	58	26/3/2017 6:21	60
21/3/2017 1:01	59	22/3/2017 2:06	58	23/3/2017 3:11	59	24/3/2017 4:16	57	25/3/2017 5:21	59	26/3/2017 6:26	45
21/3/2017 1:06	61	22/3/2017 2:11	58	23/3/2017 3:16	59	24/3/2017 4:21	56	25/3/2017 5:26	59	26/3/2017 6:31	39
21/3/2017 1:11	61	22/3/2017 2:16	58	23/3/2017 3:21	59	24/3/2017 4:26	57	25/3/2017 5:31	60	26/3/2017 6:36	61
21/3/2017 1:16	60	22/3/2017 2:21	58	23/3/2017 3:26	59	24/3/2017 4:31	57	25/3/2017 5:36	59	26/3/2017 6:41	42
21/3/2017 1:21	60	22/3/2017 2:26	58	23/3/2017 3:31	59	24/3/2017 4:36	57	25/3/2017 5:41	59	26/3/2017 6:46	62
21/3/2017 1:26	60	22/3/2017 2:31	59	23/3/2017 3:36	59	24/3/2017 4:41	58	25/3/2017 5:46	59	26/3/2017 6:51	62
21/3/2017 1:31	59	22/3/2017 2:36	58	23/3/2017 3:41	58	24/3/2017 4:46	56	25/3/2017 5:51	60	26/3/2017 6:56	61
21/3/2017 1:36	61	22/3/2017 2:41	58	23/3/2017 3:46	58	24/3/2017 4:51	58	25/3/2017 5:56	60	26/3/2017 23:01	54
21/3/2017 1:41	60	22/3/2017 2:46	59	23/3/2017 3:51	58	24/3/2017 4:56	58	25/3/2017 6:01	60	26/3/2017 23:06	52
21/3/2017 1:46	59	22/3/2017 2:51	58	23/3/2017 3:56	58	24/3/2017 5:01	57	25/3/2017 6:06	60	26/3/2017 23:11	53
21/3/2017 1:51	59	22/3/2017 2:56	57	23/3/2017 4:01	57	24/3/2017 5:06	58	25/3/2017 6:11	61	26/3/2017 23:16	56
21/3/2017 1:56	58	22/3/2017 3:01	58	23/3/2017 4:06	58	24/3/2017 5:11	58	25/3/2017 6:16	61	26/3/2017 23:21	57
21/3/2017 2:01	59	22/3/2017 3:06	57	23/3/2017 4:11	58	24/3/2017 5:16	58	25/3/2017 6:21	61	26/3/2017 23:26	52
21/3/2017 2:06	58	22/3/2017 3:11	57	23/3/2017 4:16	58	24/3/2017 5:21	59	25/3/2017 6:26	62	26/3/2017 23:31	62
21/3/2017 2:11	59	22/3/2017 3:16	58	23/3/2017 4:21	58	24/3/2017 5:26	59	25/3/2017 6:31	61	26/3/2017 23:36	61
21/3/2017 2:16	58	22/3/2017 3:21	58	23/3/2017 4:26	58	24/3/2017 5:31	58	25/3/2017 6:36	48	26/3/2017 23:41	50
21/3/2017 2:21	59	22/3/2017 3:26	58	23/3/2017 4:31	57	24/3/2017 5:36	59	25/3/2017 6:41	47	26/3/2017 23:46	48
21/3/2017 2:26	58	22/3/2017 3:31	57	23/3/2017 4:36	58	24/3/2017 5:41	58	25/3/2017 6:46	45	26/3/2017 23:51	49
21/3/2017 2:31	59	22/3/2017 3:36	58	23/3/2017 4:41	57	24/3/2017 5:46	60	25/3/2017 6:51	56	26/3/2017 23:56	48
21/3/2017 2:36	58	22/3/2017 3:41	58	23/3/2017 4:46	58	24/3/2017 5:51	60	25/3/2017 6:56	55		
21/3/2017 2:41	57	22/3/2017 3:46	58	23/3/2017 4:51	58	24/3/2017 5:56	61	25/3/20			

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)											
Normal Day 07:00-19:00													
		3/3/2017 12:31	77	9/3/2017 7:01	59	14/3/2017 13:31	66	20/3/2017 8:01	63	24/3/2017 14:31	54		
		3/3/2017 13:01	78	9/3/2017 7:31	65	14/3/2017 14:01	66	20/3/2017 8:31	65	24/3/2017 15:01	66		
27/2/2017 7:01	64	3/3/2017 13:31	76	9/3/2017 8:01	67	14/3/2017 14:31	66	20/3/2017 9:01	66	24/3/2017 15:31	66		
27/2/2017 7:31	73	3/3/2017 14:01	75	9/3/2017 8:31	63	14/3/2017 15:01	66	20/3/2017 9:31	67	24/3/2017 16:01	67		
27/2/2017 8:01	77	3/3/2017 14:31	75	9/3/2017 9:01	67	14/3/2017 15:31	65	20/3/2017 10:01	66	24/3/2017 16:31	65		
27/2/2017 8:31	79	3/3/2017 15:01	74	9/3/2017 9:31	68	14/3/2017 16:01	54	20/3/2017 10:31	67	24/3/2017 17:01	63		
27/2/2017 9:01	79	3/3/2017 15:31	-	9/3/2017 10:01	70	14/3/2017 16:31	66	20/3/2017 11:01	67	24/3/2017 17:31	61		
27/2/2017 9:31	79	3/3/2017 16:01	66	9/3/2017 10:31	62	14/3/2017 17:01	65	20/3/2017 11:31	65	24/3/2017 18:01	61		
27/2/2017 10:01	80	3/3/2017 16:31	67	9/3/2017 11:01	62	14/3/2017 17:31	60	20/3/2017 12:01	62	24/3/2017 18:31	61		
27/2/2017 10:31	77	3/3/2017 17:01	54	9/3/2017 11:31	66	14/3/2017 18:01	58	20/3/2017 12:31	63	25/3/2017 7:01	58		
27/2/2017 11:01	75	3/3/2017 17:31	65	9/3/2017 12:01	61	14/3/2017 18:31	59	20/3/2017 13:01	65	25/3/2017 7:31	62		
27/2/2017 11:31	78	3/3/2017 18:01	66	9/3/2017 12:31	60	15/3/2017 7:01	57	20/3/2017 13:31	67	25/3/2017 8:01	58		
27/2/2017 12:01	75	3/3/2017 18:31	63	9/3/2017 13:01	65	15/3/2017 7:31	60	20/3/2017 14:01	67	25/3/2017 8:31	68		
27/2/2017 12:31	76	4/3/2017 7:01	60	9/3/2017 13:31	66	15/3/2017 8:01	65	20/3/2017 14:31	65	25/3/2017 9:01	67		
27/2/2017 13:01	75	4/3/2017 7:31	65	9/3/2017 14:01	66	15/3/2017 8:31	65	20/3/2017 15:01	65	25/3/2017 9:31	67		
27/2/2017 13:31	77	4/3/2017 8:01	62	9/3/2017 14:31	65	15/3/2017 9:01	65	20/3/2017 15:31	65	25/3/2017 10:01	68		
27/2/2017 14:01	76	4/3/2017 8:31	63	9/3/2017 15:01	65	15/3/2017 9:31	66	20/3/2017 16:01	65	25/3/2017 10:31	74		
27/2/2017 14:31	75	4/3/2017 9:01	66	9/3/2017 15:31	65	15/3/2017 10:01	66	20/3/2017 16:31	64	25/3/2017 11:01	59		
27/2/2017 15:01	74	4/3/2017 9:31	63	9/3/2017 16:01	65	15/3/2017 10:31	65	20/3/2017 17:01	62	25/3/2017 11:31	64		
27/2/2017 15:31	78	4/3/2017 10:01	62	9/3/2017 16:31	64	15/3/2017 11:01	65	20/3/2017 17:31	61	25/3/2017 12:01	62		
27/2/2017 16:01	77	4/3/2017 10:31	43	9/3/2017 17:01	64	15/3/2017 11:31	63	20/3/2017 18:01	60	25/3/2017 12:31	62		
27/2/2017 16:31	76	4/3/2017 11:01	62	9/3/2017 17:31	60	15/3/2017 12:01	60	20/3/2017 18:31	59	25/3/2017 13:01	66		
27/2/2017 17:01	74	4/3/2017 11:31	65	9/3/2017 18:01	60	15/3/2017 12:31	63	21/3/2017 7:01	58	25/3/2017 13:31	55		
27/2/2017 17:31	71	4/3/2017 12:01	61	9/3/2017 18:31	58	15/3/2017 13:01	65	21/3/2017 7:31	62	25/3/2017 14:01	52		
27/2/2017 18:01	72	4/3/2017 12:31	62	10/3/2017 7:01	58	15/3/2017 13:31	67	21/3/2017 8:01	63	25/3/2017 14:31	61		
27/2/2017 18:31	73	4/3/2017 13:01	61	10/3/2017 7:31	61	15/3/2017 14:01	66	21/3/2017 8:31	65	25/3/2017 15:01	57		
28/2/2017 7:01	61	4/3/2017 13:31	68	10/3/2017 8:01	63	15/3/2017 14:31	66	21/3/2017 9:01	66	25/3/2017 15:31	67		
28/2/2017 7:31	75	4/3/2017 14:01	67	10/3/2017 8:31	65	15/3/2017 15:01	64	21/3/2017 9:31	66	25/3/2017 16:01	66		
28/2/2017 8:01	76	4/3/2017 14:31	67	10/3/2017 9:01	66	15/3/2017 15:31	64	21/3/2017 10:01	65	25/3/2017 16:31	66		
28/2/2017 8:31	75	4/3/2017 15:01	67	10/3/2017 9:31	67	15/3/2017 16:01	65	21/3/2017 10:31	67	25/3/2017 17:01	63		
28/2/2017 9:01	76	4/3/2017 15:31	49	10/3/2017 10:01	66	15/3/2017 16:31	64	21/3/2017 11:01	67	25/3/2017 17:31	60		
28/2/2017 9:31	77	4/3/2017 16:01	66	10/3/2017 10:31	51	15/3/2017 17:01	63	21/3/2017 11:31	57	25/3/2017 18:01	59		
28/2/2017 10:01	77	4/3/2017 16:31	64	10/3/2017 11:01	67	15/3/2017 17:31	60	21/3/2017 12:01	61	25/3/2017 18:31	58		
28/2/2017 10:31	78	4/3/2017 17:01	62	10/3/2017 11:31	63	15/3/2017 18:01	60	21/3/2017 12:31	62				
28/2/2017 11:01	78	4/3/2017 17:31	62	10/3/2017 12:01	61	15/3/2017 18:31	60	21/3/2017 13:01	66	Normal Day 19:00-23:00			
28/2/2017 11:31	77	4/3/2017 18:01	61	10/3/2017 12:31	63	16/3/2017 7:01	57	21/3/2017 13:31	66	Sunday & Holiday			
28/2/2017 12:01	70	4/3/2017 18:31	60	10/3/2017 13:01	66	16/3/2017 7:31	61	21/3/2017 14:01	67	07:00-23:00			
28/2/2017 12:31	70	6/3/2017 7:01	59	10/3/2017 13:31	67	16/3/2017 8:01	64	21/3/2017 14:31	65	27/2/2017 19:01	59		
28/2/2017 13:01	71	6/3/2017 7:31	62	10/3/2017 14:01	49	16/3/2017 8:31	66	21/3/2017 15:01	65	27/2/2017 19:06	60		
28/2/2017 13:31	75	6/3/2017 8:01	65	10/3/2017 14:31	65	16/3/2017 9:01	62	21/3/2017 15:31	65	27/2/2017 19:11	57		
28/2/2017 14:01	74	6/3/2017 8:31	65	10/3/2017 15:01	66	16/3/2017 9:31	56	21/3/2017 16:01	65	27/2/2017 19:16	57		
28/2/2017 14:31	72	6/3/2017 9:01	49	10/3/2017 15:31	65	16/3/2017 10:01	67	21/3/2017 16:31	65	27/2/2017 19:21	56		
28/2/2017 15:01	73	6/3/2017 9:31	66	10/3/2017 16:01	65	16/3/2017 10:31	69	21/3/2017 17:01	63	27/2/2017 19:26	58		
28/2/2017 15:31	72	6/3/2017 10:01	66	10/3/2017 16:31	63	16/3/2017 11:01	62	21/3/2017 17:31	61	27/2/2017 19:31	57		
28/2/2017 16:01	76	6/3/2017 10:31	66	10/3/2017 17:01	62	16/3/2017 11:31	62	21/3/2017 18:01	60	27/2/2017 19:36	59		
28/2/2017 16:31	75	6/3/2017 11:01	65	10/3/2017 17:31	61	16/3/2017 12:01	61	21/3/2017 18:31	60	27/2/2017 19:41	57		
28/2/2017 17:01	73	6/3/2017 11:31	65	10/3/2017 18:01	61	16/3/2017 12:31	61	22/3/2017 7:01	59	27/2/2017 19:46	56		
28/2/2017 17:31	66	6/3/2017 12:01	62	10/3/2017 18:31	61	16/3/2017 13:01	66	22/3/2017 7:31	65	27/2/2017 19:51	57		
28/2/2017 18:01	66	6/3/2017 12:31	62	11/3/2017 7:01	57	16/3/2017 13:31	67	22/3/2017 8:01	68	27/2/2017 19:56	59		
28/2/2017 18:31	67	6/3/2017 13:01	65	11/3/2017 7:31	62	16/3/2017 14:01	67	22/3/2017 8:31	68	27/2/2017 20:01	56		
1/3/2017 7:01	60	6/3/2017 13:31	66	11/3/2017 8:01	64	16/3/2017 14:31	67	22/3/2017 9:01	66	27/2/2017 20:06	56		
1/3/2017 7:31	65	6/3/2017 14:01	66	11/3/2017 8:31	66	16/3/2017 15:01	66	22/3/2017 9:31	67	27/2/2017 20:11	56		
1/3/2017 8:01	70	6/3/2017 14:31	67	11/3/2017 9:01	67	16/3/2017 15:31	66	22/3/2017 10:01	65	27/2/2017 20:16	58		
1/3/2017 8:31	75	6/3/2017 15:01	65	11/3/2017 9:31	66	16/3/2017 16:01	66	22/3/2017 10:31	65	27/2/2017 20:21	57		
1/3/2017 9:01	75	6/3/2017 15:31	65	11/3/2017 10:01	65	16/3/2017 16:31	64	22/3/2017 11:01	69	27/2/2017 20:26	57		
1/3/2017 9:31	75	6/3/2017 16:01	64	11/3/2017 10:31	67	16/3/2017 17:01	62	22/3/2017 11:31	65	27/2/2017 20:31	56		
1/3/2017 10:01	78	6/3/2017 16:31	64	11/3/2017 11:01	66	16/3/2017 17:31	61	22/3/2017 12:01	66	27/2/2017 20:36	57		
1/3/2017 10:31	76	6/3/2017 17:01	61	11/3/2017 11:31	68	16/3/2017 18:01	62	22/3/2017 12:31	66	27/2/2017 20:41	59		
1/3/2017 11:01	74	6/3/2017 17:31	61	11/3/2017 12:01	64	16/3/2017 18:31	59	22/3/2017 13:01	51	27/2/2017 20:46	59		
1/3/2017 11:31	73	6/3/2017 18:01	61	11/3/2017 12:31	62	17/3/2017 7:01	57	22/3/2017 13:31	63	27/2/2017 20:51	57		
1/3/2017 12:01	68	6/3/2017 18:31	59	11/3/2017 13:01	65	17/3/2017 7:31	63	22/3/2017 14:01	66	27/2/2017 20:56	59		
1/3/2017 12:31	69	7/3/2017 7:01	59	11/3/2017 13:31	52	17/3/2017 8:01	66	22/3/2017 14:31	65	27/2/2017 21:01	59		
1/3/2017 13:01	75	7/3/2017 7:31	61	11/3/2017 14:01	64	17/3/2017 8:31	64	22/3/2017 15:01	66	27/2/2017 21:06	56		
1/3/2017 13:31	75	7/3/2017 8:01	63	11/3/2017 14:31	67	17/3/2017 9:01	65	22/3/2017 15:31	56	27/2/2017 21:11	55		
1/3/2017 14:01	75	7/3/2017 8:31	70	11/3/2017 15:01	66	17/3/2017 9:31	67	22/3/2017 16:01	67	27/2/2017 21:16	56		
1/3/2017 14:31	74	7/3/2017 9:01	72	11/3/2017 15:31	64	17/3/2017 10:01	63	22/3/2017 16:31	66	27/2/2017 21:21	56		
1/3/2017 15:01	76	7/3/2017 9:31	74	11/3/2017 16:01	65	17/3/2017 10:31	64	22/3/2017 17:01	65	27/2/2017 21:26	55		
1/3/2017 15:31	74	7/3/2017 10:01	72	11/3/2017 16:31	66	17/3/2017 11:01	64	22/3/2017 17:31	62	27/2/2017 21:31	55		
1/3/2017 16:01	73	7/3/2017 10:31	67	11/3/2017 17:01	63	17/3/2017 11:31	62	22/3/2017 18:01	63	27/2/2017 21:36	56		
1/3/2017 16:31	69	7/3/2017 11:01	62	11/3/2017 17:31	62	17/3/2017 12:01	62	22/3/2017 18:31	61	27/2/2017 21:41	55		
1/3/2017 17:01	67	7/3/2017 11:31	66	11/3/2017 18:01	61	17/3/2							

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)											
28/2/2017 20:56	55	2/3/2017 22:01	57	5/3/2017 7:06	57	5/3/2017 16:11	58	6/3/2017 21:16	56	8/3/2017 22:21	56		
28/2/2017 21:01	59	2/3/2017 22:06	55	5/3/2017 7:11	55	5/3/2017 16:16	57	6/3/2017 21:21	56	8/3/2017 22:26	56		
28/2/2017 21:06	61	2/3/2017 22:11	57	5/3/2017 7:16	57	5/3/2017 16:21	58	6/3/2017 21:26	55	8/3/2017 22:31	57		
28/2/2017 21:11	56	2/3/2017 22:16	57	5/3/2017 7:21	57	5/3/2017 16:26	58	6/3/2017 21:31	55	8/3/2017 22:36	55		
28/2/2017 21:16	55	2/3/2017 22:21	59	5/3/2017 7:26	56	5/3/2017 16:31	58	6/3/2017 21:36	56	8/3/2017 22:41	55		
28/2/2017 21:21	56	2/3/2017 22:26	57	5/3/2017 7:31	56	5/3/2017 16:36	59	6/3/2017 21:41	56	8/3/2017 22:46	55		
28/2/2017 21:26	57	2/3/2017 22:31	57	5/3/2017 7:36	58	5/3/2017 16:41	58	6/3/2017 21:46	55	8/3/2017 22:51	56		
28/2/2017 21:31	56	2/3/2017 22:36	58	5/3/2017 7:41	61	5/3/2017 16:46	58	6/3/2017 21:51	55	8/3/2017 22:56	55		
28/2/2017 21:36	55	2/3/2017 22:41	57	5/3/2017 7:46	57	5/3/2017 16:51	58	6/3/2017 21:56	56	9/3/2017 19:01	58		
28/2/2017 21:41	62	2/3/2017 22:46	57	5/3/2017 7:51	57	5/3/2017 16:56	58	6/3/2017 22:01	56	9/3/2017 19:06	58		
28/2/2017 21:46	56	2/3/2017 22:51	57	5/3/2017 7:56	59	5/3/2017 17:01	59	6/3/2017 22:06	57	9/3/2017 19:11	57		
28/2/2017 21:51	56	2/3/2017 22:56	58	5/3/2017 8:01	57	5/3/2017 17:06	59	6/3/2017 22:11	55	9/3/2017 19:16	58		
28/2/2017 21:56	59	3/3/2017 19:01	60	5/3/2017 8:06	56	5/3/2017 17:11	60	6/3/2017 22:16	58	9/3/2017 19:21	57		
28/2/2017 22:01	57	3/3/2017 19:06	58	5/3/2017 8:11	56	5/3/2017 17:16	59	6/3/2017 22:21	57	9/3/2017 19:26	59		
28/2/2017 22:06	59	3/3/2017 19:11	54	5/3/2017 8:16	58	5/3/2017 17:21	58	6/3/2017 22:26	56	9/3/2017 19:31	59		
28/2/2017 22:11	56	3/3/2017 19:16	60	5/3/2017 8:21	58	5/3/2017 17:26	57	6/3/2017 22:31	57	9/3/2017 19:36	60		
28/2/2017 22:16	57	3/3/2017 19:21	58	5/3/2017 8:26	60	5/3/2017 17:31	58	6/3/2017 22:36	58	9/3/2017 19:41	59		
28/2/2017 22:21	60	3/3/2017 19:26	59	5/3/2017 8:31	58	5/3/2017 17:36	59	6/3/2017 22:41	57	9/3/2017 19:46	57		
28/2/2017 22:26	56	3/3/2017 19:31	59	5/3/2017 8:36	58	5/3/2017 17:41	58	6/3/2017 22:46	55	9/3/2017 19:51	58		
28/2/2017 22:31	61	3/3/2017 19:36	59	5/3/2017 8:41	59	5/3/2017 17:46	58	6/3/2017 22:51	56	9/3/2017 19:56	57		
28/2/2017 22:36	57	3/3/2017 19:41	59	5/3/2017 8:46	59	5/3/2017 17:51	58	6/3/2017 22:56	55	9/3/2017 20:01	57		
28/2/2017 22:41	58	3/3/2017 19:46	59	5/3/2017 8:51	57	5/3/2017 17:56	58	7/3/2017 19:01	59	9/3/2017 20:06	56		
28/2/2017 22:46	56	3/3/2017 19:51	60	5/3/2017 8:56	59	5/3/2017 18:01	58	7/3/2017 19:06	58	9/3/2017 20:11	56		
28/2/2017 22:51	59	3/3/2017 19:56	57	5/3/2017 9:01	60	5/3/2017 18:06	58	7/3/2017 19:11	59	9/3/2017 20:16	59		
28/2/2017 22:56	55	3/3/2017 20:01	58	5/3/2017 9:06	57	5/3/2017 18:11	59	7/3/2017 19:16	59	9/3/2017 20:21	58		
1/3/2017 19:01	60	3/3/2017 20:06	59	5/3/2017 9:11	57	5/3/2017 18:16	59	7/3/2017 19:21	58	9/3/2017 20:26	57		
1/3/2017 19:06	57	3/3/2017 20:11	50	5/3/2017 9:16	59	5/3/2017 18:21	59	7/3/2017 19:26	58	9/3/2017 20:31	59		
1/3/2017 19:11	56	3/3/2017 20:16	59	5/3/2017 9:21	59	5/3/2017 18:26	58	7/3/2017 19:31	60	9/3/2017 20:36	57		
1/3/2017 19:16	56	3/3/2017 20:21	60	5/3/2017 9:26	58	5/3/2017 18:31	57	7/3/2017 19:36	58	9/3/2017 20:41	56		
1/3/2017 19:21	56	3/3/2017 20:26	57	5/3/2017 9:31	59	5/3/2017 18:36	59	7/3/2017 19:41	60	9/3/2017 20:46	56		
1/3/2017 19:26	56	3/3/2017 20:31	59	5/3/2017 9:36	59	5/3/2017 18:41	62	7/3/2017 19:46	59	9/3/2017 20:51	56		
1/3/2017 19:31	57	3/3/2017 20:36	59	5/3/2017 9:41	60	5/3/2017 18:46	59	7/3/2017 19:51	58	9/3/2017 20:56	56		
1/3/2017 19:36	57	3/3/2017 20:41	58	5/3/2017 9:46	59	5/3/2017 18:51	58	7/3/2017 19:56	58	9/3/2017 21:01	55		
1/3/2017 19:41	57	3/3/2017 20:46	62	5/3/2017 9:51	59	5/3/2017 18:56	59	7/3/2017 20:01	59	9/3/2017 21:06	55		
1/3/2017 19:46	57	3/3/2017 20:51	58	5/3/2017 9:56	59	5/3/2017 19:01	57	7/3/2017 20:06	58	9/3/2017 21:11	57		
1/3/2017 19:51	57	3/3/2017 20:56	57	5/3/2017 10:01	49	5/3/2017 19:06	58	7/3/2017 20:11	58	9/3/2017 21:16	58		
1/3/2017 19:56	56	3/3/2017 21:01	58	5/3/2017 10:06	59	5/3/2017 19:11	58	7/3/2017 20:16	59	9/3/2017 21:21	57		
1/3/2017 20:01	56	3/3/2017 21:06	57	5/3/2017 10:11	58	5/3/2017 19:16	57	7/3/2017 20:21	59	9/3/2017 21:26	55		
1/3/2017 20:06	56	3/3/2017 21:11	58	5/3/2017 10:16	61	5/3/2017 19:21	58	7/3/2017 20:26	59	9/3/2017 21:31	56		
1/3/2017 20:11	56	3/3/2017 21:16	62	5/3/2017 10:21	59	5/3/2017 19:26	58	7/3/2017 20:31	57	9/3/2017 21:36	57		
1/3/2017 20:16	56	3/3/2017 21:21	57	5/3/2017 10:26	59	5/3/2017 19:31	60	7/3/2017 20:36	59	9/3/2017 21:41	57		
1/3/2017 20:21	56	3/3/2017 21:26	58	5/3/2017 10:31	60	5/3/2017 19:36	59	7/3/2017 20:41	59	9/3/2017 21:46	55		
1/3/2017 20:26	57	3/3/2017 21:31	58	5/3/2017 10:36	60	5/3/2017 19:41	57	7/3/2017 20:46	59	9/3/2017 21:51	56		
1/3/2017 20:31	56	3/3/2017 21:36	58	5/3/2017 10:41	59	5/3/2017 19:46	58	7/3/2017 20:51	58	9/3/2017 21:56	55		
1/3/2017 20:36	57	3/3/2017 21:41	57	5/3/2017 10:46	60	5/3/2017 19:51	58	7/3/2017 20:56	60	9/3/2017 22:01	55		
1/3/2017 20:41	55	3/3/2017 21:46	59	5/3/2017 10:51	60	5/3/2017 19:56	57	7/3/2017 21:01	61	9/3/2017 22:06	55		
1/3/2017 20:46	56	3/3/2017 21:51	58	5/3/2017 10:56	59	5/3/2017 20:01	58	7/3/2017 21:06	59	9/3/2017 22:11	56		
1/3/2017 20:51	56	3/3/2017 21:56	59	5/3/2017 11:01	59	5/3/2017 20:06	57	7/3/2017 21:11	59	9/3/2017 22:16	55		
1/3/2017 20:56	56	3/3/2017 22:01	57	5/3/2017 11:06	60	5/3/2017 20:11	58	7/3/2017 21:16	59	9/3/2017 22:21	58		
1/3/2017 21:01	56	3/3/2017 22:06	57	5/3/2017 11:11	59	5/3/2017 20:16	59	7/3/2017 21:21	61	9/3/2017 22:26	56		
1/3/2017 21:06	55	3/3/2017 22:11	57	5/3/2017 11:16	61	5/3/2017 20:21	58	7/3/2017 21:26	59	9/3/2017 22:31	55		
1/3/2017 21:11	55	3/3/2017 22:16	59	5/3/2017 11:21	59	5/3/2017 20:26	57	7/3/2017 21:31	60	9/3/2017 22:36	55		
1/3/2017 21:16	57	3/3/2017 22:21	57	5/3/2017 11:26	60	5/3/2017 20:31	57	7/3/2017 21:36	60	9/3/2017 22:41	55		
1/3/2017 21:21	58	3/3/2017 22:26	57	5/3/2017 11:31	60	5/3/2017 20:36	57	7/3/2017 21:41	59	9/3/2017 22:46	56		
1/3/2017 21:26	56	3/3/2017 22:31	57	5/3/2017 11:36	58	5/3/2017 20:41	57	7/3/2017 21:46	60	9/3/2017 22:51	58		
1/3/2017 21:31	58	3/3/2017 22:36	57	5/3/2017 11:41	60	5/3/2017 20:46	58	7/3/2017 21:51	60	9/3/2017 22:56	59		
1/3/2017 21:36	57	3/3/2017 22:41	58	5/3/2017 11:46	59	5/3/2017 20:51	57	7/3/2017 21:56	60	10/3/2017 19:01	59		
1/3/2017 21:41	58	3/3/2017 22:46	58	5/3/2017 11:51	58	5/3/2017 20:56	58	7/3/2017 22:01	60	10/3/2017 19:06	59		
1/3/2017 21:46	57	3/3/2017 22:51	58	5/3/2017 11:56	58	5/3/2017 21:01	58	7/3/2017 22:06	60	10/3/2017 19:11	57		
1/3/2017 21:51	57	3/3/2017 22:56	57	5/3/2017 12:01	58	5/3/2017 21:06	58	7/3/2017 22:11	60	10/3/2017 19:16	57		
1/3/2017 21:56	55	4/3/2017 19:01	60	5/3/2017 12:06	59	5/3/2017 21:11	57	7/3/2017 22:16	61	10/3/2017 19:21	58		
1/3/2017 22:01	55	4/3/2017 19:06	58	5/3/2017 12:11	60	5/3/2017 21:16	58	7/3/2017 22:21	61	10/3/2017 19:26	58		
1/3/2017 22:06	57	4/3/2017 19:11	60	5/3/2017 12:16	60	5/3/2017 21:21	58	7/3/2017 22:26	61	10/3/2017 19:31	59		
1/3/2017 22:11	57	4/3/2017 19:16	59	5/3/2017 12:21	58	5/3/2017 21:26	59	7/3/2017 22:31	61	10/3/2017 19:36	58		
1/3/2017 22:16	59	4/3/2017 19:21	58	5/3/2017 12:26	58	5/3/2017 21:31	59	7/3/2017 22:36	60	10/3/2017 19:41	59		
1/3/2017 22:21	57	4/3/2017 19:26	58	5/3/2017 12:31	57	5/3/2017 21:36	57	7/3/2017 22:41	62	10/3/2017 19:46	59		
1/3/2017 22:26	59	4/3/2017 19:31	60	5/3/2017 12:36	59	5/3/2017 21:41	58	7/3/2017 22:46	61	10/3/2017 19:51	58		
1/3/2017 22:31	56	4/3/2017 19:36	60	5/3/2017 12:41	58	5/3/2017 21:46	57	7/3/2017 22:51	59	10/3/2017 19:56	58		
1/3/2017 22:36	62	4/3/2017 19:41	60	5/3/2017 12:46	59	5/3/2017 21:51	57	7/3/2017 22:56	59	10/3/2017 20:01	57		
1/3/2017 22:41	56	4/3/2017 19:46	59	5/3/2017 12:51	59	5/3/2017 21:56	57	8/3/2017 19:01	51	10/3/2017 20:06	59		
1/3/2017 22:46	57	4/3/2017 19:51	57	5/3/2017 12:56	59	5/3/2017 22:01	56	8/3/2017 19:06	57	10/3/2017 20:11	58		
1/3/2017 22:51	57	4/3/2017 19:56	58	5/3/2017 13:01	58	5/3/2017 22:06	56	8/3/2017 19:11	57	10/3/2017 20:16	61		
1/3													

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
11/3/2017 19:26	62	12/3/2017 12:31	57	12/3/2017 21:36	56	14/3/2017 22:41	58	17/3/2017 19:46	59	19/3/2017 8:51	59
11/3/2017 19:31	62	12/3/2017 12:36	57	12/3/2017 21:41	57	14/3/2017 22:46	56	17/3/2017 19:51	59	19/3/2017 8:56	57
11/3/2017 19:36	59	12/3/2017 12:41	57	12/3/2017 21:46	56	14/3/2017 22:51	56	17/3/2017 19:56	57	19/3/2017 9:01	56
11/3/2017 19:41	60	12/3/2017 12:46	58	12/3/2017 21:51	57	14/3/2017 22:56	56	17/3/2017 20:01	59	19/3/2017 9:06	58
11/3/2017 19:46	61	12/3/2017 12:51	60	12/3/2017 21:56	57	15/3/2017 19:01	60	17/3/2017 20:06	57	19/3/2017 9:11	58
11/3/2017 19:51	58	12/3/2017 12:56	59	12/3/2017 22:01	57	15/3/2017 19:06	58	17/3/2017 20:11	61	19/3/2017 9:16	58
11/3/2017 19:56	61	12/3/2017 13:01	56	12/3/2017 22:06	57	15/3/2017 19:11	57	17/3/2017 20:16	57	19/3/2017 9:21	58
11/3/2017 20:01	60	12/3/2017 13:06	56	12/3/2017 22:11	56	15/3/2017 19:16	57	17/3/2017 20:21	58	19/3/2017 9:26	58
11/3/2017 20:06	60	12/3/2017 13:11	57	12/3/2017 22:16	57	15/3/2017 19:21	58	17/3/2017 20:26	57	19/3/2017 9:31	58
11/3/2017 20:11	59	12/3/2017 13:16	56	12/3/2017 22:21	60	15/3/2017 19:26	58	17/3/2017 20:31	57	19/3/2017 9:36	58
11/3/2017 20:16	58	12/3/2017 13:21	57	12/3/2017 22:26	58	15/3/2017 19:31	61	17/3/2017 20:36	59	19/3/2017 9:41	58
11/3/2017 20:21	58	12/3/2017 13:26	58	12/3/2017 22:31	57	15/3/2017 19:36	58	17/3/2017 20:41	59	19/3/2017 9:46	57
11/3/2017 20:26	59	12/3/2017 13:31	58	12/3/2017 22:36	58	15/3/2017 19:41	60	17/3/2017 20:46	57	19/3/2017 9:51	58
11/3/2017 20:31	61	12/3/2017 13:36	57	12/3/2017 22:41	58	15/3/2017 19:46	61	17/3/2017 20:51	57	19/3/2017 9:56	57
11/3/2017 20:36	54	12/3/2017 13:41	61	12/3/2017 22:46	56	15/3/2017 19:51	60	17/3/2017 20:56	58	19/3/2017 10:01	58
11/3/2017 20:41	58	12/3/2017 13:46	57	12/3/2017 22:51	57	15/3/2017 19:56	58	17/3/2017 21:01	57	19/3/2017 10:06	58
11/3/2017 20:46	58	12/3/2017 13:51	57	12/3/2017 22:56	57	15/3/2017 20:01	57	17/3/2017 21:06	56	19/3/2017 10:11	57
11/3/2017 20:51	60	12/3/2017 13:56	58	13/3/2017 19:01	61	15/3/2017 20:06	59	17/3/2017 21:11	56	19/3/2017 10:16	57
11/3/2017 20:56	59	12/3/2017 14:01	57	13/3/2017 19:06	60	15/3/2017 20:11	60	17/3/2017 21:16	56	19/3/2017 10:21	58
11/3/2017 21:01	58	12/3/2017 14:06	57	13/3/2017 19:11	58	15/3/2017 20:16	59	17/3/2017 21:21	57	19/3/2017 10:26	58
11/3/2017 21:06	60	12/3/2017 14:11	57	13/3/2017 19:16	57	15/3/2017 20:21	57	17/3/2017 21:26	57	19/3/2017 10:31	57
11/3/2017 21:11	58	12/3/2017 14:16	57	13/3/2017 19:21	59	15/3/2017 20:26	61	17/3/2017 21:31	57	19/3/2017 10:36	57
11/3/2017 21:16	61	12/3/2017 14:21	58	13/3/2017 19:26	59	15/3/2017 20:31	58	17/3/2017 21:36	57	19/3/2017 10:41	57
11/3/2017 21:21	61	12/3/2017 14:26	57	13/3/2017 19:31	58	15/3/2017 20:36	57	17/3/2017 21:41	56	19/3/2017 10:46	57
11/3/2017 21:26	58	12/3/2017 14:31	57	13/3/2017 19:36	60	15/3/2017 20:41	56	17/3/2017 21:46	57	19/3/2017 10:51	58
11/3/2017 21:31	57	12/3/2017 14:36	57	13/3/2017 19:41	59	15/3/2017 20:46	57	17/3/2017 21:51	56	19/3/2017 10:56	57
11/3/2017 21:36	56	12/3/2017 14:41	56	13/3/2017 19:46	62	15/3/2017 20:51	56	17/3/2017 21:56	57	19/3/2017 11:01	58
11/3/2017 21:41	58	12/3/2017 14:46	57	13/3/2017 19:51	43	15/3/2017 20:56	57	17/3/2017 22:01	57	19/3/2017 11:06	58
11/3/2017 21:46	57	12/3/2017 14:51	57	13/3/2017 19:56	57	15/3/2017 21:01	59	17/3/2017 22:06	57	19/3/2017 11:11	59
11/3/2017 21:51	58	12/3/2017 14:56	58	13/3/2017 20:01	58	15/3/2017 21:06	57	17/3/2017 22:11	56	19/3/2017 11:16	58
11/3/2017 21:56	58	12/3/2017 15:01	56	13/3/2017 20:06	53	15/3/2017 21:11	57	17/3/2017 22:16	57	19/3/2017 11:21	57
11/3/2017 22:01	58	12/3/2017 15:06	58	13/3/2017 20:11	58	15/3/2017 21:16	57	17/3/2017 22:21	56	19/3/2017 11:26	57
11/3/2017 22:06	57	12/3/2017 15:11	60	13/3/2017 20:16	61	15/3/2017 21:21	56	17/3/2017 22:26	59	19/3/2017 11:31	57
11/3/2017 22:11	57	12/3/2017 15:16	57	13/3/2017 20:21	58	15/3/2017 21:26	57	17/3/2017 22:31	57	19/3/2017 11:36	58
11/3/2017 22:16	59	12/3/2017 15:21	59	13/3/2017 20:26	59	15/3/2017 21:31	56	17/3/2017 22:36	57	19/3/2017 11:41	57
11/3/2017 22:21	57	12/3/2017 15:26	58	13/3/2017 20:31	59	15/3/2017 21:36	56	17/3/2017 22:41	58	19/3/2017 11:46	58
11/3/2017 22:26	57	12/3/2017 15:31	58	13/3/2017 20:36	61	15/3/2017 21:41	57	17/3/2017 22:46	56	19/3/2017 11:51	57
11/3/2017 22:31	58	12/3/2017 15:36	56	13/3/2017 20:41	59	15/3/2017 21:46	57	17/3/2017 22:51	55	19/3/2017 11:56	58
11/3/2017 22:36	57	12/3/2017 15:41	58	13/3/2017 20:46	59	15/3/2017 21:51	59	17/3/2017 22:56	57	19/3/2017 12:01	58
11/3/2017 22:41	58	12/3/2017 15:46	57	13/3/2017 20:51	57	15/3/2017 21:56	57	18/3/2017 19:01	59	19/3/2017 12:06	58
11/3/2017 22:46	56	12/3/2017 15:51	56	13/3/2017 20:56	56	15/3/2017 22:01	56	18/3/2017 19:06	58	19/3/2017 12:11	58
11/3/2017 22:51	57	12/3/2017 15:56	58	13/3/2017 21:01	57	15/3/2017 22:06	58	18/3/2017 19:11	57	19/3/2017 12:16	59
11/3/2017 22:56	56	12/3/2017 16:01	57	13/3/2017 21:06	56	15/3/2017 22:11	58	18/3/2017 19:16	57	19/3/2017 12:21	60
12/3/2017 7:01	56	12/3/2017 16:06	57	13/3/2017 21:11	56	15/3/2017 22:16	57	18/3/2017 19:21	58	19/3/2017 12:26	59
12/3/2017 7:06	55	12/3/2017 16:11	57	13/3/2017 21:16	57	15/3/2017 22:21	60	18/3/2017 19:26	57	19/3/2017 12:31	62
12/3/2017 7:11	56	12/3/2017 16:16	57	13/3/2017 21:21	57	15/3/2017 22:26	60	18/3/2017 19:31	59	19/3/2017 12:36	58
12/3/2017 7:16	55	12/3/2017 16:21	56	13/3/2017 21:26	57	15/3/2017 22:31	59	18/3/2017 19:36	57	19/3/2017 12:41	60
12/3/2017 7:21	55	12/3/2017 16:26	57	13/3/2017 21:31	56	15/3/2017 22:36	57	18/3/2017 19:41	58	19/3/2017 12:46	59
12/3/2017 7:26	57	12/3/2017 16:31	60	13/3/2017 21:36	57	15/3/2017 22:41	56	18/3/2017 19:46	57	19/3/2017 12:51	60
12/3/2017 7:31	55	12/3/2017 16:36	57	13/3/2017 21:41	57	15/3/2017 22:46	57	18/3/2017 19:51	56	19/3/2017 12:56	59
12/3/2017 7:36	55	12/3/2017 16:41	57	13/3/2017 21:46	58	15/3/2017 22:51	55	18/3/2017 19:56	58	19/3/2017 13:01	58
12/3/2017 7:41	57	12/3/2017 16:46	58	13/3/2017 21:51	57	15/3/2017 22:56	57	18/3/2017 20:01	57	19/3/2017 13:06	58
12/3/2017 7:46	55	12/3/2017 16:51	57	13/3/2017 21:56	57	16/3/2017 19:01	61	18/3/2017 20:06	59	19/3/2017 13:11	53
12/3/2017 7:51	56	12/3/2017 16:56	58	13/3/2017 22:01	57	16/3/2017 19:06	59	18/3/2017 20:11	58	19/3/2017 13:16	58
12/3/2017 7:56	58	12/3/2017 17:01	58	13/3/2017 22:06	57	16/3/2017 19:11	57	18/3/2017 20:16	57	19/3/2017 13:21	60
12/3/2017 8:01	57	12/3/2017 17:06	56	13/3/2017 22:11	58	16/3/2017 19:16	60	18/3/2017 20:21	58	19/3/2017 13:26	58
12/3/2017 8:06	57	12/3/2017 17:11	59	13/3/2017 22:16	57	16/3/2017 19:21	59	18/3/2017 20:26	59	19/3/2017 13:31	58
12/3/2017 8:11	57	12/3/2017 17:16	56	13/3/2017 22:21	58	16/3/2017 19:26	57	18/3/2017 20:31	58	19/3/2017 13:36	60
12/3/2017 8:16	58	12/3/2017 17:21	57	13/3/2017 22:26	57	16/3/2017 19:31	58	18/3/2017 20:36	56	19/3/2017 13:41	58
12/3/2017 8:21	57	12/3/2017 17:26	57	13/3/2017 22:31	59	16/3/2017 19:36	61	18/3/2017 20:41	59	19/3/2017 13:46	59
12/3/2017 8:26	59	12/3/2017 17:31	59	13/3/2017 22:36	58	16/3/2017 19:41	61	18/3/2017 20:46	58	19/3/2017 13:51	58
12/3/2017 8:31	58	12/3/2017 17:36	57	13/3/2017 22:41	56	16/3/2017 19:46	61	18/3/2017 20:51	57	19/3/2017 13:56	58
12/3/2017 8:36	59	12/3/2017 17:41	57	13/3/2017 22:46	58	16/3/2017 19:51	61	18/3/2017 20:56	58	19/3/2017 14:01	58
12/3/2017 8:41	57	12/3/2017 17:46	60	13/3/2017 22:51	57	16/3/2017 19:56	59	18/3/2017 21:01	58	19/3/2017 14:06	58
12/3/2017 8:46	58	12/3/2017 17:51	58	13/3/2017 22:56	57	16/3/2017 20:01	60	18/3/2017 21:06	56	19/3/2017 14:11	57
12/3/2017 8:51	58	12/3/2017 17:56	57	14/3/2017 19:01	46	16/3/2017 20:06	56	18/3/2017 21:11	56	19/3/2017 14:16	50
12/3/2017 8:56	58	12/3/2017 18:01	58	14/3/2017 19:06	57	16/3/2017 20:11	60	18/3/2017 21:16	58	19/3/2017 14:21	57
12/3/2017 9:01	58	12/3/2017 18:06	58	14/3/2017 19:11	57	16/3/2017 20:16	61	18/3/2017 21:21	57	19/3/2017 14:26	57
12/3/2017 9:06	58	12/3/2017 18:11	58	14/3/2017 19:16	57	16/3/2017 20:21	60	18/3/2017 21:26	59	19/3/2017 14:31	60
12/3/2017 9:11	58	12/3/2017 18:16	58	14/3/2017 19:21	57	16/3/2017 20:26	58	18/3/2017 21:31	56	19/3/2017 14:36	57
12/3/2017 9:16	58	12/3/2017 18:21	60	14/3/2017 19:26	57	16/3/2017 20:31	61	18/3/2017 21:36	56	19/3/2017 14:41	58
12/3/2017 9:21	58	12/3/2017 18:26	58	14/3/2017 19:31	61	16/3/2017 20:36	60	18/3/2017 21:41	56	19/3/2017 14:46	58
12/3/2017 9:26	58	12/3/2017 18:31	58	14/3/2017 19:36	59	16/3/2017 20:41	58	18/3/2017 21:46	56	19/3/2017 14:51	60
12/3/2017 9:31	58	12/3/2017 18:36	57								

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
19/3/2017 17:56	56	21/3/2017 19:01	59	23/3/2017 20:06	58	25/3/2017 21:11	60	26/3/2017 14:16	59	Night time: 23:00-07:00	
19/3/2017 18:01	57	21/3/2017 19:06	58	23/3/2017 20:11	58	25/3/2017 21:16	56	26/3/2017 14:21	57		
19/3/2017 18:06	59	21/3/2017 19:11	59	23/3/2017 20:16	59	25/3/2017 21:21	56	26/3/2017 14:26	57	27/2/2017 0:01	54
19/3/2017 18:11	57	21/3/2017 19:16	58	23/3/2017 20:21	59	25/3/2017 21:26	56	26/3/2017 14:31	58	27/2/2017 0:06	53
19/3/2017 18:16	55	21/3/2017 19:21	59	23/3/2017 20:26	61	25/3/2017 21:31	55	26/3/2017 14:36	58	27/2/2017 0:11	53
19/3/2017 18:21	57	21/3/2017 19:26	58	23/3/2017 20:31	57	25/3/2017 21:36	57	26/3/2017 14:41	56	27/2/2017 0:16	53
19/3/2017 18:26	60	21/3/2017 19:31	60	23/3/2017 20:36	60	25/3/2017 21:41	56	26/3/2017 14:46	60	27/2/2017 0:21	53
19/3/2017 18:31	57	21/3/2017 19:36	61	23/3/2017 20:41	57	25/3/2017 21:46	56	26/3/2017 14:51	58	27/2/2017 0:26	53
19/3/2017 18:36	56	21/3/2017 19:41	57	23/3/2017 20:46	58	25/3/2017 21:51	57	26/3/2017 14:56	57	27/2/2017 0:31	52
19/3/2017 18:41	59	21/3/2017 19:46	58	23/3/2017 20:51	58	25/3/2017 21:56	58	26/3/2017 15:01	57	27/2/2017 0:36	52
19/3/2017 18:46	57	21/3/2017 19:51	59	23/3/2017 20:56	57	25/3/2017 22:01	59	26/3/2017 15:06	58	27/2/2017 0:41	56
19/3/2017 18:51	58	21/3/2017 19:56	58	23/3/2017 21:01	57	25/3/2017 22:06	59	26/3/2017 15:11	61	27/2/2017 0:46	51
19/3/2017 18:56	57	21/3/2017 20:01	57	23/3/2017 21:06	60	25/3/2017 22:11	56	26/3/2017 15:16	58	27/2/2017 0:51	53
19/3/2017 19:01	57	21/3/2017 20:06	58	23/3/2017 21:11	56	25/3/2017 22:16	56	26/3/2017 15:21	57	27/2/2017 0:56	52
19/3/2017 19:06	57	21/3/2017 20:11	57	23/3/2017 21:16	57	25/3/2017 22:21	57	26/3/2017 15:26	57	27/2/2017 1:01	52
19/3/2017 19:11	57	21/3/2017 20:16	58	23/3/2017 21:21	56	25/3/2017 22:26	57	26/3/2017 15:31	57	27/2/2017 1:06	52
19/3/2017 19:16	57	21/3/2017 20:21	59	23/3/2017 21:26	61	25/3/2017 22:31	56	26/3/2017 15:36	58	27/2/2017 1:11	52
19/3/2017 19:21	57	21/3/2017 20:26	57	23/3/2017 21:31	56	25/3/2017 22:36	58	26/3/2017 15:41	57	27/2/2017 1:16	52
19/3/2017 19:26	57	21/3/2017 20:31	57	23/3/2017 21:36	56	25/3/2017 22:41	59	26/3/2017 15:46	57	27/2/2017 1:21	52
19/3/2017 19:31	58	21/3/2017 20:36	59	23/3/2017 21:41	57	25/3/2017 22:46	59	26/3/2017 15:51	57	27/2/2017 1:26	52
19/3/2017 19:36	58	21/3/2017 20:41	57	23/3/2017 21:46	57	25/3/2017 22:51	56	26/3/2017 15:56	57	27/2/2017 1:31	52
19/3/2017 19:41	58	21/3/2017 20:46	57	23/3/2017 21:51	59	25/3/2017 22:56	57	26/3/2017 16:01	53	27/2/2017 1:36	51
19/3/2017 19:46	59	21/3/2017 20:51	57	23/3/2017 21:56	57	26/3/2017 7:01	55	26/3/2017 16:06	58	27/2/2017 1:41	51
19/3/2017 19:51	56	21/3/2017 20:56	56	23/3/2017 22:01	58	26/3/2017 7:06	55	26/3/2017 16:11	59	27/2/2017 1:46	53
19/3/2017 19:56	56	21/3/2017 21:01	56	23/3/2017 22:06	57	26/3/2017 7:11	55	26/3/2017 16:16	57	27/2/2017 1:51	52
19/3/2017 20:01	56	21/3/2017 21:06	56	23/3/2017 22:11	61	26/3/2017 7:16	55	26/3/2017 16:21	58	27/2/2017 1:56	52
19/3/2017 20:06	58	21/3/2017 21:11	56	23/3/2017 22:16	57	26/3/2017 7:21	55	26/3/2017 16:26	58	27/2/2017 2:01	52
19/3/2017 20:11	58	21/3/2017 21:16	56	23/3/2017 22:21	58	26/3/2017 7:26	56	26/3/2017 16:31	60	27/2/2017 2:06	51
19/3/2017 20:16	57	21/3/2017 21:21	56	23/3/2017 22:26	58	26/3/2017 7:31	59	26/3/2017 16:36	57	27/2/2017 2:11	51
19/3/2017 20:21	60	21/3/2017 21:26	55	23/3/2017 22:31	60	26/3/2017 7:36	57	26/3/2017 16:41	57	27/2/2017 2:16	53
19/3/2017 20:26	58	21/3/2017 21:31	56	23/3/2017 22:36	57	26/3/2017 7:41	57	26/3/2017 16:46	59	27/2/2017 2:21	51
19/3/2017 20:31	58	21/3/2017 21:36	56	23/3/2017 22:41	57	26/3/2017 7:46	56	26/3/2017 16:51	59	27/2/2017 2:26	52
19/3/2017 20:36	57	21/3/2017 21:41	57	23/3/2017 22:46	57	26/3/2017 7:51	55	26/3/2017 16:56	60	27/2/2017 2:31	50
19/3/2017 20:41	56	21/3/2017 21:46	56	23/3/2017 22:51	56	26/3/2017 7:56	58	26/3/2017 17:01	59	27/2/2017 2:36	53
19/3/2017 20:46	56	21/3/2017 21:51	56	23/3/2017 22:56	59	26/3/2017 8:01	56	26/3/2017 17:06	58	27/2/2017 2:41	50
19/3/2017 20:51	56	21/3/2017 21:56	56	24/3/2017 19:01	57	26/3/2017 8:06	58	26/3/2017 17:11	57	27/2/2017 2:46	50
19/3/2017 20:56	56	21/3/2017 22:01	56	24/3/2017 19:06	58	26/3/2017 8:11	56	26/3/2017 17:16	59	27/2/2017 2:51	51
19/3/2017 21:01	57	21/3/2017 22:06	56	24/3/2017 19:11	59	26/3/2017 8:16	57	26/3/2017 17:21	58	27/2/2017 2:56	52
19/3/2017 21:06	56	21/3/2017 22:11	56	24/3/2017 19:16	59	26/3/2017 8:21	58	26/3/2017 17:26	58	27/2/2017 3:01	51
19/3/2017 21:11	56	21/3/2017 22:16	56	24/3/2017 19:21	58	26/3/2017 8:26	58	26/3/2017 17:31	58	27/2/2017 3:06	50
19/3/2017 21:16	56	21/3/2017 22:21	56	24/3/2017 19:26	58	26/3/2017 8:31	58	26/3/2017 17:36	60	27/2/2017 3:11	50
19/3/2017 21:21	57	21/3/2017 22:26	56	24/3/2017 19:31	60	26/3/2017 8:36	57	26/3/2017 17:41	58	27/2/2017 3:16	49
19/3/2017 21:26	56	21/3/2017 22:31	56	24/3/2017 19:36	58	26/3/2017 8:41	57	26/3/2017 17:46	58	27/2/2017 3:21	49
19/3/2017 21:31	56	21/3/2017 22:36	56	24/3/2017 19:41	60	26/3/2017 8:46	57	26/3/2017 17:51	56	27/2/2017 3:26	51
19/3/2017 21:36	57	21/3/2017 22:41	57	24/3/2017 19:46	62	26/3/2017 8:51	57	26/3/2017 17:56	57	27/2/2017 3:31	50
19/3/2017 21:41	57	21/3/2017 22:46	56	24/3/2017 19:51	57	26/3/2017 8:56	60	26/3/2017 18:01	62	27/2/2017 3:36	50
19/3/2017 21:46	56	21/3/2017 22:51	55	24/3/2017 19:56	62	26/3/2017 9:01	59	26/3/2017 18:06	57	27/2/2017 3:41	49
19/3/2017 21:51	56	21/3/2017 22:56	57	24/3/2017 20:01	60	26/3/2017 9:06	60	26/3/2017 18:11	59	27/2/2017 3:46	49
19/3/2017 21:56	58	22/3/2017 19:01	61	24/3/2017 20:06	58	26/3/2017 9:11	60	26/3/2017 18:16	60	27/2/2017 3:51	50
19/3/2017 22:01	56	22/3/2017 19:06	58	24/3/2017 20:11	59	26/3/2017 9:16	60	26/3/2017 18:21	57	27/2/2017 3:56	50
19/3/2017 22:06	56	22/3/2017 19:11	59	24/3/2017 20:16	60	26/3/2017 9:21	57	26/3/2017 18:26	57	27/2/2017 4:01	50
19/3/2017 22:11	56	22/3/2017 19:16	59	24/3/2017 20:21	59	26/3/2017 9:26	60	26/3/2017 18:31	57	27/2/2017 4:06	50
19/3/2017 22:16	56	22/3/2017 19:21	60	24/3/2017 20:26	59	26/3/2017 9:31	59	26/3/2017 18:36	57	27/2/2017 4:11	50
19/3/2017 22:21	57	22/3/2017 19:26	58	24/3/2017 20:31	59	26/3/2017 9:36	57	26/3/2017 18:41	57	27/2/2017 4:16	50
19/3/2017 22:26	57	22/3/2017 19:31	60	24/3/2017 20:36	57	26/3/2017 9:41	58	26/3/2017 18:46	53	27/2/2017 4:21	50
19/3/2017 22:31	55	22/3/2017 19:36	59	24/3/2017 20:41	57	26/3/2017 9:46	59	26/3/2017 18:51	60	27/2/2017 4:26	50
19/3/2017 22:36	55	22/3/2017 19:41	59	24/3/2017 20:46	57	26/3/2017 9:51	59	26/3/2017 18:56	59	27/2/2017 4:31	50
19/3/2017 22:41	55	22/3/2017 19:46	59	24/3/2017 20:51	56	26/3/2017 9:56	58	26/3/2017 19:01	58	27/2/2017 4:36	50
19/3/2017 22:46	56	22/3/2017 19:51	58	24/3/2017 20:56	56	26/3/2017 10:01	61	26/3/2017 19:06	58	27/2/2017 4:41	49
19/3/2017 22:51	55	22/3/2017 19:56	58	24/3/2017 21:01	57	26/3/2017 10:06	59	26/3/2017 19:11	59	27/2/2017 4:46	50
19/3/2017 22:56	55	22/3/2017 20:01	60	24/3/2017 21:06	60	26/3/2017 10:11	59	26/3/2017 19:16	57	27/2/2017 4:51	51
20/3/2017 19:01	59	22/3/2017 20:06	58	24/3/2017 21:11	58	26/3/2017 10:16	58	26/3/2017 19:21	59	27/2/2017 4:56	49
20/3/2017 19:06	59	22/3/2017 20:11	59	24/3/2017 21:16	56	26/3/2017 10:21	58	26/3/2017 19:26	59	27/2/2017 5:01	50
20/3/2017 19:11	58	22/3/2017 20:16	62	24/3/2017 21:21	56	26/3/2017 10:26	59	26/3/2017 19:31	59	27/2/2017 5:06	51
20/3/2017 19:16	59	22/3/2017 20:21	61	24/3/2017 21:26	56	26/3/2017 10:31	58	26/3/2017 19:36	61	27/2/2017 5:11	51
20/3/2017 19:21	59	22/3/2017 20:26	59	24/3/2017 21:31	57	26/3/2017 10:36	57	26/3/2017 19:41	57	27/2/2017 5:16	51
20/3/2017 19:26	59	22/3/2017 20:31	59	24/3/2017 21:36	57	26/3/2017 10:41	58	26/3/2017 19:46	59	27/2/2017 5:21	50
20/3/2017 19:31	60	22/3/2017 20:36	58	24/3/2017 21:41	57	26/3/2017 10:46	60	26/3/2017 19:51	59	27/2/2017 5:26	51
20/3/2017 19:36	60	22/3/2017 20:41	58	24/3/2017 21:46	56	26/3/2017 10:51	57	26/3/2017 19:56	57	27/2/2017 5:31	51
20/3/2017 19:41	58	22/3/2017 20:46	57	24/3/2017 21:51	56	26/3/2017 10:56	58	26/3/2017 20:01	57	27/2/2017 5:36	50
20/3/2017 19:46	58	22/3/2017 20:51	57	24/3/2017 21:56	58	26/3/2017 11:01	58	26/3/2017 20:06	57	27/2/2017 5:41	51
20/3/2017 19:51	58	22/3/2017 20:56	58	24/3/2017 22:01	56	26/3/2017 11:06	59	26/3/2017 20:11	57	27/2/2017 5:46	50
20/3/2017 19:56	57	22/3/2017 21:01	57	24/3/2017 22:06	60	26/3/2017 11:11	58	26/3/2017 20:16	58	27/2/2017 5:51	52
20/3/2017 20:01	58	22/3/2017 21:06	56								

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)											
28/2/2017 0:56	62	1/3/2017 2:01	52	2/3/2017 3:06	53	3/3/2017 4:11	54	4/3/2017 5:16	53	5/3/2017 6:21	56		
28/2/2017 1:01	53	1/3/2017 2:06	52	2/3/2017 3:11	54	3/3/2017 4:16	54	4/3/2017 5:21	54	5/3/2017 6:26	55		
28/2/2017 1:06	39	1/3/2017 2:11	51	2/3/2017 3:16	54	3/3/2017 4:21	54	4/3/2017 5:26	56	5/3/2017 6:31	43		
28/2/2017 1:11	52	1/3/2017 2:16	50	2/3/2017 3:21	52	3/3/2017 4:26	56	4/3/2017 5:31	54	5/3/2017 6:36	55		
28/2/2017 1:16	52	1/3/2017 2:21	51	2/3/2017 3:26	53	3/3/2017 4:31	53	4/3/2017 5:36	54	5/3/2017 6:41	56		
28/2/2017 1:21	52	1/3/2017 2:26	52	2/3/2017 3:31	53	3/3/2017 4:36	53	4/3/2017 5:41	54	5/3/2017 6:46	56		
28/2/2017 1:26	52	1/3/2017 2:31	50	2/3/2017 3:36	51	3/3/2017 4:41	54	4/3/2017 5:46	56	5/3/2017 6:51	55		
28/2/2017 1:31	52	1/3/2017 2:36	50	2/3/2017 3:41	53	3/3/2017 4:46	53	4/3/2017 5:51	54	5/3/2017 6:56	56		
28/2/2017 1:36	53	1/3/2017 2:41	53	2/3/2017 3:46	53	3/3/2017 4:51	54	4/3/2017 5:56	54	5/3/2017 23:01	57		
28/2/2017 1:41	52	1/3/2017 2:46	51	2/3/2017 3:51	53	3/3/2017 4:56	50	4/3/2017 6:01	54	5/3/2017 23:06	56		
28/2/2017 1:46	51	1/3/2017 2:51	51	2/3/2017 3:56	55	3/3/2017 5:01	51	4/3/2017 6:06	54	5/3/2017 23:11	58		
28/2/2017 1:51	51	1/3/2017 2:56	51	2/3/2017 4:01	53	3/3/2017 5:06	51	4/3/2017 6:11	55	5/3/2017 23:16	57		
28/2/2017 1:56	52	1/3/2017 3:01	51	2/3/2017 4:06	53	3/3/2017 5:11	50	4/3/2017 6:16	54	5/3/2017 23:21	57		
28/2/2017 2:01	51	1/3/2017 3:06	51	2/3/2017 4:11	53	3/3/2017 5:16	51	4/3/2017 6:21	55	5/3/2017 23:26	57		
28/2/2017 2:06	50	1/3/2017 3:11	51	2/3/2017 4:16	52	3/3/2017 5:21	52	4/3/2017 6:26	55	5/3/2017 23:31	56		
28/2/2017 2:11	52	1/3/2017 3:16	50	2/3/2017 4:21	53	3/3/2017 5:26	51	4/3/2017 6:31	54	5/3/2017 23:36	56		
28/2/2017 2:16	51	1/3/2017 3:21	50	2/3/2017 4:26	52	3/3/2017 5:31	52	4/3/2017 6:36	56	5/3/2017 23:41	57		
28/2/2017 2:21	52	1/3/2017 3:26	52	2/3/2017 4:31	53	3/3/2017 5:36	53	4/3/2017 6:41	55	5/3/2017 23:46	54		
28/2/2017 2:26	51	1/3/2017 3:31	57	2/3/2017 4:36	52	3/3/2017 5:41	51	4/3/2017 6:46	55	5/3/2017 23:51	57		
28/2/2017 2:31	50	1/3/2017 3:36	51	2/3/2017 4:41	53	3/3/2017 5:46	51	4/3/2017 6:51	56	5/3/2017 23:56	55		
28/2/2017 2:36	51	1/3/2017 3:41	52	2/3/2017 4:46	54	3/3/2017 5:51	52	4/3/2017 6:56	57	6/3/2017 0:01	55		
28/2/2017 2:41	51	1/3/2017 3:46	51	2/3/2017 4:51	55	3/3/2017 5:56	52	4/3/2017 23:01	56	6/3/2017 0:06	56		
28/2/2017 2:46	51	1/3/2017 3:51	51	2/3/2017 4:56	55	3/3/2017 6:01	52	4/3/2017 23:06	56	6/3/2017 0:11	57		
28/2/2017 2:51	50	1/3/2017 3:56	50	2/3/2017 5:01	54	3/3/2017 6:06	51	4/3/2017 23:11	57	6/3/2017 0:16	55		
28/2/2017 2:56	50	1/3/2017 4:01	50	2/3/2017 5:06	54	3/3/2017 6:11	52	4/3/2017 23:16	57	6/3/2017 0:21	54		
28/2/2017 3:01	52	1/3/2017 4:06	50	2/3/2017 5:11	52	3/3/2017 6:16	54	4/3/2017 23:21	56	6/3/2017 0:26	55		
28/2/2017 3:06	54	1/3/2017 4:11	51	2/3/2017 5:16	52	3/3/2017 6:21	54	4/3/2017 23:26	57	6/3/2017 0:31	56		
28/2/2017 3:11	51	1/3/2017 4:16	51	2/3/2017 5:21	54	3/3/2017 6:26	54	4/3/2017 23:31	56	6/3/2017 0:36	54		
28/2/2017 3:16	50	1/3/2017 4:21	50	2/3/2017 5:26	52	3/3/2017 6:31	54	4/3/2017 23:36	56	6/3/2017 0:41	54		
28/2/2017 3:21	51	1/3/2017 4:26	51	2/3/2017 5:31	54	3/3/2017 6:36	55	4/3/2017 23:41	56	6/3/2017 0:46	53		
28/2/2017 3:26	50	1/3/2017 4:31	50	2/3/2017 5:36	54	3/3/2017 6:41	55	4/3/2017 23:46	56	6/3/2017 0:51	57		
28/2/2017 3:31	51	1/3/2017 4:36	50	2/3/2017 5:41	55	3/3/2017 6:46	54	4/3/2017 23:51	56	6/3/2017 0:56	55		
28/2/2017 3:36	51	1/3/2017 4:41	49	2/3/2017 5:46	54	3/3/2017 6:51	56	4/3/2017 23:56	57	6/3/2017 1:01	56		
28/2/2017 3:41	50	1/3/2017 4:46	51	2/3/2017 5:51	54	3/3/2017 6:56	56	5/3/2017 0:01	56	6/3/2017 1:06	55		
28/2/2017 3:46	51	1/3/2017 4:51	50	2/3/2017 5:56	55	3/3/2017 23:01	56	5/3/2017 0:06	56	6/3/2017 1:11	54		
28/2/2017 3:51	52	1/3/2017 4:56	51	2/3/2017 6:01	53	3/3/2017 23:06	56	5/3/2017 0:11	58	6/3/2017 1:16	53		
28/2/2017 3:56	51	1/3/2017 5:01	51	2/3/2017 6:06	53	3/3/2017 23:11	57	5/3/2017 0:16	56	6/3/2017 1:21	55		
28/2/2017 4:01	50	1/3/2017 5:06	52	2/3/2017 6:11	54	3/3/2017 23:16	56	5/3/2017 0:21	56	6/3/2017 1:26	55		
28/2/2017 4:06	50	1/3/2017 5:11	51	2/3/2017 6:16	54	3/3/2017 23:21	56	5/3/2017 0:26	55	6/3/2017 1:31	55		
28/2/2017 4:11	50	1/3/2017 5:16	50	2/3/2017 6:21	56	3/3/2017 23:26	57	5/3/2017 0:31	56	6/3/2017 1:36	55		
28/2/2017 4:16	50	1/3/2017 5:21	51	2/3/2017 6:26	56	3/3/2017 23:31	57	5/3/2017 0:36	56	6/3/2017 1:41	55		
28/2/2017 4:21	52	1/3/2017 5:26	52	2/3/2017 6:31	56	3/3/2017 23:36	56	5/3/2017 0:41	56	6/3/2017 1:46	56		
28/2/2017 4:26	51	1/3/2017 5:31	51	2/3/2017 6:36	56	3/3/2017 23:41	57	5/3/2017 0:46	55	6/3/2017 1:51	54		
28/2/2017 4:31	50	1/3/2017 5:36	52	2/3/2017 6:41	56	3/3/2017 23:46	58	5/3/2017 0:51	56	6/3/2017 1:56	54		
28/2/2017 4:36	49	1/3/2017 5:41	52	2/3/2017 6:46	56	3/3/2017 23:51	56	5/3/2017 0:56	56	6/3/2017 2:01	56		
28/2/2017 4:41	50	1/3/2017 5:46	51	2/3/2017 6:51	56	3/3/2017 23:56	56	5/3/2017 1:01	55	6/3/2017 2:06	54		
28/2/2017 4:46	49	1/3/2017 5:51	52	2/3/2017 6:56	56	4/3/2017 0:01	55	5/3/2017 1:06	55	6/3/2017 2:11	55		
28/2/2017 4:51	50	1/3/2017 5:56	52	2/3/2017 23:01	57	4/3/2017 0:06	56	5/3/2017 1:11	55	6/3/2017 2:16	51		
28/2/2017 4:56	51	1/3/2017 6:01	51	2/3/2017 23:06	57	4/3/2017 0:11	56	5/3/2017 1:16	55	6/3/2017 2:21	54		
28/2/2017 5:01	51	1/3/2017 6:06	52	2/3/2017 23:11	56	4/3/2017 0:16	56	5/3/2017 1:21	56	6/3/2017 2:26	54		
28/2/2017 5:06	51	1/3/2017 6:11	52	2/3/2017 23:16	56	4/3/2017 0:21	56	5/3/2017 1:26	57	6/3/2017 2:31	53		
28/2/2017 5:11	50	1/3/2017 6:16	54	2/3/2017 23:21	56	4/3/2017 0:26	56	5/3/2017 1:31	55	6/3/2017 2:36	52		
28/2/2017 5:16	52	1/3/2017 6:21	54	2/3/2017 23:26	56	4/3/2017 0:31	58	5/3/2017 1:36	55	6/3/2017 2:41	55		
28/2/2017 5:21	52	1/3/2017 6:26	54	2/3/2017 23:31	55	4/3/2017 0:36	56	5/3/2017 1:41	55	6/3/2017 2:46	55		
28/2/2017 5:26	51	1/3/2017 6:31	54	2/3/2017 23:36	55	4/3/2017 0:41	55	5/3/2017 1:46	54	6/3/2017 2:51	54		
28/2/2017 5:31	51	1/3/2017 6:36	53	2/3/2017 23:41	55	4/3/2017 0:46	55	5/3/2017 1:51	55	6/3/2017 2:56	54		
28/2/2017 5:36	52	1/3/2017 6:41	54	2/3/2017 23:46	56	4/3/2017 0:51	56	5/3/2017 1:56	55	6/3/2017 3:01	57		
28/2/2017 5:41	51	1/3/2017 6:46	54	2/3/2017 23:51	56	4/3/2017 0:56	55	5/3/2017 2:01	55	6/3/2017 3:06	54		
28/2/2017 5:46	51	1/3/2017 6:51	56	2/3/2017 23:56	55	4/3/2017 1:01	56	5/3/2017 2:06	55	6/3/2017 3:11	54		
28/2/2017 5:51	52	1/3/2017 6:56	55	3/3/2017 0:01	56	4/3/2017 1:06	56	5/3/2017 2:11	54	6/3/2017 3:16	54		
28/2/2017 5:56	53	1/3/2017 23:01	55	3/3/2017 0:06	55	4/3/2017 1:11	55	5/3/2017 2:16	54	6/3/2017 3:21	55		
28/2/2017 6:01	52	1/3/2017 23:06	55	3/3/2017 0:11	55	4/3/2017 1:16	56	5/3/2017 2:21	56	6/3/2017 3:26	54		
28/2/2017 6:06	53	1/3/2017 23:11	55	3/3/2017 0:16	55	4/3/2017 1:21	55	5/3/2017 2:26	55	6/3/2017 3:31	54		
28/2/2017 6:11	54	1/3/2017 23:16	55	3/3/2017 0:21	55	4/3/2017 1:26	55	5/3/2017 2:31	55	6/3/2017 3:36	55		
28/2/2017 6:16	53	1/3/2017 23:21	54	3/3/2017 0:26	56	4/3/2017 1:31	54	5/3/2017 2:36	54	6/3/2017 3:41	55		
28/2/2017 6:21	53	1/3/2017 23:26	55	3/3/2017 0:31	55	4/3/2017 1:36	55	5/3/2017 2:41	54	6/3/2017 3:46	52		
28/2/2017 6:26	54	1/3/2017 23:31	55	3/3/2017 0:36	54	4/3/2017 1:41	55	5/3/2017 2:46	54	6/3/2017 3:51	53		
28/2/2017 6:31	53	1/3/2017 23:36	55	3/3/2017 0:41	55	4/3/2017 1:46	58	5/3/2017 2:51	55	6/3/2017 3:56	53		
28/2/2017 6:36	54	1/3/2017 23:41	56	3/3/2017 0:46	56	4/3/2017 1:51	55	5/3/2017 2:56	55	6/3/2017 4:01	54		
28/2/2017 6:41	54	1/3/2017 23:46	55	3/3/2017 0:51	55	4/3/2017 1:56	56	5/3/2017 3:01	54	6/3/2017 4:06	55		
28/2/2017 6:46	55	1/3/2017 23:51	55	3/3/2017 0:56	54	4/3/2017 2:01	54	5/3/2017 3:06	55	6/3/2017 4:11	54		
28/2/2017 6:51	57	1/3/2017 23:56	55	3/3/2017 1:01	53	4/3/2017 2:06	54	5/3/2017 3:11	54	6/3/2017 4:16	53		
28/2/2017 6:56	56	2/3/2017 0:01	55	3/3/2017 1:06	52	4/3/2017 2:11	54	5/3/2017 3:16	54	6/3/2017 4:21	55		
28/2/2017 23:01	56	2/3/2017 0:06	55	3/3/2017 1:11	53	4/3/2017 2:16	54	5/3/2017 3:21	55	6/3/2017 4:26			

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)											
6/3/2017 23:26	57	8/3/2017 0:31	57	9/3/2017 1:36	52	10/3/2017 2:41	54	11/3/2017 3:46	54	12/3/2017 4:51	52		
6/3/2017 23:31	52	8/3/2017 0:36	57	9/3/2017 1:41	54	10/3/2017 2:46	53	11/3/2017 3:51	53	12/3/2017 4:56	53		
6/3/2017 23:36	57	8/3/2017 0:41	57	9/3/2017 1:46	54	10/3/2017 2:51	54	11/3/2017 3:56	54	12/3/2017 5:01	52		
6/3/2017 23:41	58	8/3/2017 0:46	57	9/3/2017 1:51	54	10/3/2017 2:56	54	11/3/2017 4:01	53	12/3/2017 5:06	54		
6/3/2017 23:46	58	8/3/2017 0:51	57	9/3/2017 1:56	54	10/3/2017 3:01	52	11/3/2017 4:06	54	12/3/2017 5:11	54		
6/3/2017 23:51	35	8/3/2017 0:56	56	9/3/2017 2:01	53	10/3/2017 3:06	52	11/3/2017 4:11	54	12/3/2017 5:16	54		
6/3/2017 23:56	53	8/3/2017 1:01	58	9/3/2017 2:06	53	10/3/2017 3:11	53	11/3/2017 4:16	54	12/3/2017 5:21	53		
7/3/2017 0:01	58	8/3/2017 1:06	57	9/3/2017 2:11	52	10/3/2017 3:16	53	11/3/2017 4:21	53	12/3/2017 5:26	54		
7/3/2017 0:06	58	8/3/2017 1:11	57	9/3/2017 2:16	53	10/3/2017 3:21	52	11/3/2017 4:26	53	12/3/2017 5:31	53		
7/3/2017 0:11	58	8/3/2017 1:16	56	9/3/2017 2:21	53	10/3/2017 3:26	53	11/3/2017 4:31	53	12/3/2017 5:36	53		
7/3/2017 0:16	58	8/3/2017 1:21	56	9/3/2017 2:26	55	10/3/2017 3:31	52	11/3/2017 4:36	53	12/3/2017 5:41	54		
7/3/2017 0:21	57	8/3/2017 1:26	57	9/3/2017 2:31	52	10/3/2017 3:36	53	11/3/2017 4:41	54	12/3/2017 5:46	54		
7/3/2017 0:26	58	8/3/2017 1:31	56	9/3/2017 2:36	52	10/3/2017 3:41	54	11/3/2017 4:46	53	12/3/2017 5:51	54		
7/3/2017 0:31	58	8/3/2017 1:36	57	9/3/2017 2:41	53	10/3/2017 3:46	54	11/3/2017 4:51	53	12/3/2017 5:56	54		
7/3/2017 0:36	44	8/3/2017 1:41	57	9/3/2017 2:46	52	10/3/2017 3:51	52	11/3/2017 4:56	53	12/3/2017 6:01	54		
7/3/2017 0:41	58	8/3/2017 1:46	58	9/3/2017 2:51	53	10/3/2017 3:56	56	11/3/2017 5:01	54	12/3/2017 6:06	53		
7/3/2017 0:46	57	8/3/2017 1:51	58	9/3/2017 2:56	53	10/3/2017 4:01	58	11/3/2017 5:06	54	12/3/2017 6:11	54		
7/3/2017 0:51	58	8/3/2017 1:56	57	9/3/2017 3:01	51	10/3/2017 4:06	56	11/3/2017 5:11	54	12/3/2017 6:16	55		
7/3/2017 0:56	57	8/3/2017 2:01	57	9/3/2017 3:06	52	10/3/2017 4:11	53	11/3/2017 5:16	53	12/3/2017 6:21	57		
7/3/2017 1:01	58	8/3/2017 2:06	58	9/3/2017 3:11	52	10/3/2017 4:16	53	11/3/2017 5:21	54	12/3/2017 6:26	55		
7/3/2017 1:06	44	8/3/2017 2:11	57	9/3/2017 3:16	52	10/3/2017 4:21	53	11/3/2017 5:26	54	12/3/2017 6:31	54		
7/3/2017 1:11	50	8/3/2017 2:16	58	9/3/2017 3:21	52	10/3/2017 4:26	52	11/3/2017 5:31	54	12/3/2017 6:36	55		
7/3/2017 1:16	47	8/3/2017 2:21	56	9/3/2017 3:26	52	10/3/2017 4:31	53	11/3/2017 5:36	55	12/3/2017 6:41	54		
7/3/2017 1:21	57	8/3/2017 2:26	56	9/3/2017 3:31	52	10/3/2017 4:36	52	11/3/2017 5:41	54	12/3/2017 6:46	55		
7/3/2017 1:26	57	8/3/2017 2:31	57	9/3/2017 3:36	52	10/3/2017 4:41	52	11/3/2017 5:46	54	12/3/2017 6:51	55		
7/3/2017 1:31	58	8/3/2017 2:36	56	9/3/2017 3:41	52	10/3/2017 4:46	52	11/3/2017 5:51	54	12/3/2017 6:56	55		
7/3/2017 1:36	58	8/3/2017 2:41	56	9/3/2017 3:46	53	10/3/2017 4:51	53	11/3/2017 5:56	54	12/3/2017 7:01	56		
7/3/2017 1:41	44	8/3/2017 2:46	56	9/3/2017 3:51	53	10/3/2017 4:56	54	11/3/2017 6:01	54	12/3/2017 7:06	56		
7/3/2017 1:46	57	8/3/2017 2:51	58	9/3/2017 3:56	51	10/3/2017 5:01	53	11/3/2017 6:06	54	12/3/2017 7:11	56		
7/3/2017 1:51	56	8/3/2017 2:56	57	9/3/2017 4:01	51	10/3/2017 5:06	56	11/3/2017 6:11	55	12/3/2017 7:16	55		
7/3/2017 1:56	57	8/3/2017 3:01	58	9/3/2017 4:06	52	10/3/2017 5:11	56	11/3/2017 6:16	55	12/3/2017 7:21	55		
7/3/2017 2:01	57	8/3/2017 3:06	57	9/3/2017 4:11	51	10/3/2017 5:16	53	11/3/2017 6:21	56	12/3/2017 7:26	55		
7/3/2017 2:06	58	8/3/2017 3:11	37	9/3/2017 4:16	52	10/3/2017 5:21	53	11/3/2017 6:26	55	12/3/2017 7:31	55		
7/3/2017 2:11	57	8/3/2017 3:16	58	9/3/2017 4:21	51	10/3/2017 5:26	53	11/3/2017 6:31	56	12/3/2017 7:36	55		
7/3/2017 2:16	58	8/3/2017 3:21	58	9/3/2017 4:26	52	10/3/2017 5:31	53	11/3/2017 6:36	56	12/3/2017 7:41	55		
7/3/2017 2:21	56	8/3/2017 3:26	56	9/3/2017 4:31	54	10/3/2017 5:36	53	11/3/2017 6:41	57	12/3/2017 7:46	55		
7/3/2017 2:26	58	8/3/2017 3:31	57	9/3/2017 4:36	52	10/3/2017 5:41	54	11/3/2017 6:46	56	12/3/2017 7:51	54		
7/3/2017 2:31	58	8/3/2017 3:36	57	9/3/2017 4:41	51	10/3/2017 5:46	54	11/3/2017 6:51	56	12/3/2017 7:56	55		
7/3/2017 2:36	57	8/3/2017 3:41	57	9/3/2017 4:46	51	10/3/2017 5:51	54	11/3/2017 6:56	55	13/3/2017 0:01	54		
7/3/2017 2:41	57	8/3/2017 3:46	57	9/3/2017 4:51	52	10/3/2017 5:56	53	11/3/2017 7:01	55	13/3/2017 0:06	55		
7/3/2017 2:46	57	8/3/2017 3:51	57	9/3/2017 4:56	52	10/3/2017 6:01	55	11/3/2017 7:06	55	13/3/2017 0:11	55		
7/3/2017 2:51	57	8/3/2017 3:56	56	9/3/2017 5:01	52	10/3/2017 6:06	54	11/3/2017 7:11	57	13/3/2017 0:16	54		
7/3/2017 2:56	58	8/3/2017 4:01	57	9/3/2017 5:06	53	10/3/2017 6:11	55	11/3/2017 7:16	56	13/3/2017 0:21	54		
7/3/2017 3:01	58	8/3/2017 4:06	57	9/3/2017 5:11	52	10/3/2017 6:16	55	11/3/2017 7:21	56	13/3/2017 0:26	54		
7/3/2017 3:06	57	8/3/2017 4:11	56	9/3/2017 5:16	52	10/3/2017 6:21	54	11/3/2017 7:26	56	13/3/2017 0:31	54		
7/3/2017 3:11	58	8/3/2017 4:16	56	9/3/2017 5:21	53	10/3/2017 6:26	55	11/3/2017 7:31	55	13/3/2017 0:36	54		
7/3/2017 3:16	57	8/3/2017 4:21	56	9/3/2017 5:26	52	10/3/2017 6:31	55	11/3/2017 7:36	55	13/3/2017 0:41	54		
7/3/2017 3:21	57	8/3/2017 4:26	55	9/3/2017 5:31	52	10/3/2017 6:36	55	11/3/2017 7:41	56	13/3/2017 0:46	54		
7/3/2017 3:26	57	8/3/2017 4:31	56	9/3/2017 5:36	51	10/3/2017 6:41	56	11/3/2017 7:46	55	13/3/2017 0:51	55		
7/3/2017 3:31	57	8/3/2017 4:36	57	9/3/2017 5:41	52	10/3/2017 6:46	56	11/3/2017 7:51	56	13/3/2017 0:56	54		
7/3/2017 3:36	57	8/3/2017 4:41	51	9/3/2017 5:46	52	10/3/2017 6:51	56	11/3/2017 7:56	56	13/3/2017 1:01	53		
7/3/2017 3:41	57	8/3/2017 4:46	58	9/3/2017 5:51	53	10/3/2017 6:56	56	12/3/2017 0:01	55	13/3/2017 1:06	53		
7/3/2017 3:46	57	8/3/2017 4:51	56	9/3/2017 5:56	52	10/3/2017 7:01	56	12/3/2017 0:06	55	13/3/2017 1:11	53		
7/3/2017 3:51	57	8/3/2017 4:56	56	9/3/2017 6:01	52	10/3/2017 7:06	57	12/3/2017 0:11	55	13/3/2017 1:16	53		
7/3/2017 3:56	57	8/3/2017 5:01	56	9/3/2017 6:06	53	10/3/2017 7:11	56	12/3/2017 0:16	55	13/3/2017 1:21	52		
7/3/2017 4:01	57	8/3/2017 5:06	57	9/3/2017 6:11	54	10/3/2017 7:16	51	12/3/2017 0:21	55	13/3/2017 1:26	53		
7/3/2017 4:06	58	8/3/2017 5:11	56	9/3/2017 6:16	54	10/3/2017 7:21	56	12/3/2017 0:26	56	13/3/2017 1:31	53		
7/3/2017 4:11	57	8/3/2017 5:16	57	9/3/2017 6:21	53	10/3/2017 7:26	57	12/3/2017 0:31	56	13/3/2017 1:36	53		
7/3/2017 4:16	58	8/3/2017 5:21	55	9/3/2017 6:26	54	10/3/2017 7:31	56	12/3/2017 0:36	55	13/3/2017 1:41	52		
7/3/2017 4:21	56	8/3/2017 5:26	56	9/3/2017 6:31	55	10/3/2017 7:36	55	12/3/2017 0:41	55	13/3/2017 1:46	53		
7/3/2017 4:26	56	8/3/2017 5:31	56	9/3/2017 6:36	54	10/3/2017 7:41	55	12/3/2017 0:46	55	13/3/2017 1:51	53		
7/3/2017 4:31	57	8/3/2017 5:36	56	9/3/2017 6:41	55	10/3/2017 7:46	55	12/3/2017 0:51	56	13/3/2017 1:56	52		
7/3/2017 4:36	57	8/3/2017 5:41	57	9/3/2017 6:46	55	10/3/2017 7:51	55	12/3/2017 0:56	55	13/3/2017 2:01	52		
7/3/2017 4:41	57	8/3/2017 5:46	57	9/3/2017 6:51	55	10/3/2017 7:56	55	12/3/2017 1:01	55	13/3/2017 2:06	52		
7/3/2017 4:46	56	8/3/2017 5:51	57	9/3/2017 6:56	56	11/3/2017 0:01	55	12/3/2017 1:06	55	13/3/2017 2:11	52		
7/3/2017 4:51	56	8/3/2017 5:56	57	9/3/2017 7:01	55	11/3/2017 0:06	55	12/3/2017 1:11	55	13/3/2017 2:16	51		
7/3/2017 4:56	56	8/3/2017 6:01	58	9/3/2017 7:06	55	11/3/2017 0:11	55	12/3/2017 1:16	55	13/3/2017 2:21	53		
7/3/2017 5:01	57	8/3/2017 6:06	58	9/3/2017 7:11	56	11/3/2017 0:16	55	12/3/2017 1:21	55	13/3/2017 2:26	51		
7/3/2017 5:06	57	8/3/2017 6:11	58	9/3/2017 7:16	56	11/3/2017 0:21	55	12/3/2017 1:26	55	13/3/2017 2:31	52		
7/3/2017 5:11	57	8/3/2017 6:16	58	9/3/2017 7:21	55	11/3/2017 0:26	56	12/3/2017 1:31	54	13/3/2017 2:36	51		
7/3/2017 5:16	57	8/3/2017 6:21	57	9/3/2017 7:26	55	11/3/2017 0:31	55	12/3/2017 1:36	54	13/3/2017 2:41	51		
7/3/2017 5:21	56	8/3/2017 6:26	57	9/3/2017 7:31	55	11/3/2017 0:36	56	12/3/2017 1:41	54	13/3/2017 2:46	52		
7/3/2017 5:26	57	8/3/2017 6:31	57	9/3/2017 7:36	55	11/3/2017 0:41	55	12/3/2017 1:46	54	13/3/2017 2:51	52		
7/3/2017 5:31	57	8/3/2017 6:36	57	9/									

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)															
13/3/2017 5:56	53	14/3/2017 23:01	57	16/3/2017 0:06	54	17/3/2017 1:11	54	18/3/2017 2:16	53	19/3/2017 3:21	54	20/3/2017 0:01	54	20/3/2017 0:06	53	20/3/2017 0:11	54
13/3/2017 6:01	53	14/3/2017 23:06	56	16/3/2017 0:11	54	17/3/2017 1:16	53	18/3/2017 2:21	54	19/3/2017 3:26	53	20/3/2017 0:16	54	20/3/2017 0:21	54	20/3/2017 0:26	54
13/3/2017 6:06	54	14/3/2017 23:11	55	16/3/2017 0:16	55	17/3/2017 1:21	53	18/3/2017 2:26	54	19/3/2017 3:31	54	20/3/2017 0:31	54	20/3/2017 0:36	54	20/3/2017 0:41	53
13/3/2017 6:11	54	14/3/2017 23:16	55	16/3/2017 0:21	55	17/3/2017 1:26	53	18/3/2017 2:31	54	19/3/2017 3:36	54	20/3/2017 0:46	54	20/3/2017 0:51	54	20/3/2017 0:56	54
13/3/2017 6:16	54	14/3/2017 23:21	55	16/3/2017 0:26	54	17/3/2017 1:31	54	18/3/2017 2:36	53	19/3/2017 3:41	53	20/3/2017 0:56	54	20/3/2017 1:01	54	20/3/2017 1:06	54
13/3/2017 6:21	54	14/3/2017 23:26	56	16/3/2017 0:31	54	17/3/2017 1:36	54	18/3/2017 2:41	54	19/3/2017 3:46	53	20/3/2017 1:06	54	20/3/2017 1:11	54	20/3/2017 1:16	54
13/3/2017 6:26	54	14/3/2017 23:31	55	16/3/2017 0:36	54	17/3/2017 1:41	53	18/3/2017 2:46	54	19/3/2017 3:51	53	20/3/2017 1:16	54	20/3/2017 1:21	54	20/3/2017 1:26	54
13/3/2017 6:31	54	14/3/2017 23:36	55	16/3/2017 0:41	53	17/3/2017 1:46	54	18/3/2017 2:51	53	19/3/2017 3:56	53	20/3/2017 1:26	54	20/3/2017 1:31	52	20/3/2017 1:36	52
13/3/2017 6:36	55	14/3/2017 23:41	55	16/3/2017 0:46	54	17/3/2017 1:51	53	18/3/2017 2:56	56	19/3/2017 4:01	53	20/3/2017 1:36	54	20/3/2017 1:41	52	20/3/2017 1:46	52
13/3/2017 6:41	55	14/3/2017 23:46	54	16/3/2017 0:51	54	17/3/2017 1:56	54	18/3/2017 3:01	54	19/3/2017 4:06	53	20/3/2017 1:46	54	20/3/2017 1:51	52	20/3/2017 1:56	52
13/3/2017 6:46	55	14/3/2017 23:51	54	16/3/2017 0:56	55	17/3/2017 2:01	52	18/3/2017 3:06	53	19/3/2017 4:11	53	20/3/2017 1:56	54	20/3/2017 2:01	50	20/3/2017 2:06	50
13/3/2017 6:51	56	14/3/2017 23:56	55	16/3/2017 1:01	54	17/3/2017 2:06	53	18/3/2017 3:11	53	19/3/2017 4:16	54	20/3/2017 2:06	54	20/3/2017 2:11	51	20/3/2017 2:16	51
13/3/2017 6:56	56	15/3/2017 0:01	55	16/3/2017 1:06	54	17/3/2017 2:11	53	18/3/2017 3:16	53	19/3/2017 4:21	56	20/3/2017 2:16	54	20/3/2017 2:21	51	20/3/2017 2:26	51
13/3/2017 23:01	56	15/3/2017 0:06	54	16/3/2017 1:11	54	17/3/2017 2:16	52	18/3/2017 3:21	53	19/3/2017 4:26	54	20/3/2017 2:26	54	20/3/2017 2:31	51	20/3/2017 2:36	51
13/3/2017 23:06	56	15/3/2017 0:11	54	16/3/2017 1:16	53	17/3/2017 2:21	53	18/3/2017 3:26	53	19/3/2017 4:31	54	20/3/2017 2:36	54	20/3/2017 2:41	51	20/3/2017 2:46	51
13/3/2017 23:11	57	15/3/2017 0:16	55	16/3/2017 1:21	53	17/3/2017 2:26	52	18/3/2017 3:31	53	19/3/2017 4:36	53	20/3/2017 2:46	54	20/3/2017 2:51	51	20/3/2017 2:56	51
13/3/2017 23:16	56	15/3/2017 0:21	55	16/3/2017 1:26	53	17/3/2017 2:31	52	18/3/2017 3:36	53	19/3/2017 4:41	53	20/3/2017 2:56	54	20/3/2017 3:01	51	20/3/2017 3:06	51
13/3/2017 23:21	55	15/3/2017 0:26	55	16/3/2017 1:31	53	17/3/2017 2:36	52	18/3/2017 3:41	54	19/3/2017 4:46	53	20/3/2017 3:06	54	20/3/2017 3:11	51	20/3/2017 3:16	51
13/3/2017 23:26	55	15/3/2017 0:31	54	16/3/2017 1:36	53	17/3/2017 2:41	52	18/3/2017 3:46	53	19/3/2017 4:51	54	20/3/2017 3:16	54	20/3/2017 3:21	51	20/3/2017 3:26	51
13/3/2017 23:31	55	15/3/2017 0:36	54	16/3/2017 1:41	54	17/3/2017 2:46	52	18/3/2017 3:51	53	19/3/2017 4:56	53	20/3/2017 3:26	54	20/3/2017 3:31	51	20/3/2017 3:36	51
13/3/2017 23:36	55	15/3/2017 0:41	54	16/3/2017 1:46	53	17/3/2017 2:51	52	18/3/2017 3:56	53	19/3/2017 5:01	54	20/3/2017 3:36	54	20/3/2017 3:41	51	20/3/2017 3:46	51
13/3/2017 23:41	56	15/3/2017 0:46	53	16/3/2017 1:51	53	17/3/2017 2:56	53	18/3/2017 4:01	53	19/3/2017 5:06	53	20/3/2017 3:46	54	20/3/2017 3:51	51	20/3/2017 3:56	51
13/3/2017 23:46	56	15/3/2017 0:51	53	16/3/2017 1:56	53	17/3/2017 3:01	52	18/3/2017 4:06	53	19/3/2017 5:11	53	20/3/2017 3:56	54	20/3/2017 4:01	51	20/3/2017 4:06	51
13/3/2017 23:51	55	15/3/2017 0:56	54	16/3/2017 2:01	52	17/3/2017 3:06	52	18/3/2017 4:11	55	19/3/2017 5:16	53	20/3/2017 4:06	54	20/3/2017 4:11	51	20/3/2017 4:16	51
13/3/2017 23:56	55	15/3/2017 1:01	54	16/3/2017 2:06	52	17/3/2017 3:11	51	18/3/2017 4:16	55	19/3/2017 5:21	53	20/3/2017 4:16	54	20/3/2017 4:21	51	20/3/2017 4:26	51
14/3/2017 0:01	55	15/3/2017 1:06	54	16/3/2017 2:11	53	17/3/2017 3:16	51	18/3/2017 4:21	55	19/3/2017 5:26	53	20/3/2017 4:26	54	20/3/2017 4:31	51	20/3/2017 4:36	51
14/3/2017 0:06	55	15/3/2017 1:11	53	16/3/2017 2:16	52	17/3/2017 3:21	54	18/3/2017 4:26	55	19/3/2017 5:31	55	20/3/2017 4:36	54	20/3/2017 4:41	51	20/3/2017 4:46	51
14/3/2017 0:11	54	15/3/2017 1:16	53	16/3/2017 2:21	52	17/3/2017 3:26	52	18/3/2017 4:31	53	19/3/2017 5:36	54	20/3/2017 4:46	54	20/3/2017 4:51	51	20/3/2017 4:56	51
14/3/2017 0:16	55	15/3/2017 1:21	53	16/3/2017 2:26	52	17/3/2017 3:31	51	18/3/2017 4:36	53	19/3/2017 5:41	54	20/3/2017 4:56	54	20/3/2017 5:01	51	20/3/2017 5:06	51
14/3/2017 0:21	54	15/3/2017 1:26	53	16/3/2017 2:31	53	17/3/2017 3:36	52	18/3/2017 4:41	53	19/3/2017 5:46	53	20/3/2017 5:06	54	20/3/2017 5:11	51	20/3/2017 5:16	51
14/3/2017 0:26	55	15/3/2017 1:31	53	16/3/2017 2:36	55	17/3/2017 3:41	52	18/3/2017 4:46	53	19/3/2017 5:51	54	20/3/2017 5:16	54	20/3/2017 5:21	51	20/3/2017 5:26	51
14/3/2017 0:31	54	15/3/2017 1:36	53	16/3/2017 2:41	52	17/3/2017 3:46	52	18/3/2017 4:51	53	19/3/2017 5:56	54	20/3/2017 5:26	54	20/3/2017 5:31	51	20/3/2017 5:36	51
14/3/2017 0:36	54	15/3/2017 1:41	53	16/3/2017 2:46	52	17/3/2017 3:51	53	18/3/2017 4:56	53	19/3/2017 6:01	54	20/3/2017 5:36	54	20/3/2017 5:41	51	20/3/2017 5:46	51
14/3/2017 0:41	55	15/3/2017 1:46	53	16/3/2017 2:51	53	17/3/2017 3:56	52	18/3/2017 5:01	54	19/3/2017 6:06	54	20/3/2017 5:46	54	20/3/2017 5:51	51	20/3/2017 5:56	51
14/3/2017 0:46	56	15/3/2017 1:51	52	16/3/2017 2:56	53	17/3/2017 4:01	52	18/3/2017 5:06	53	19/3/2017 6:11	53	20/3/2017 5:56	54	20/3/2017 6:01	51	20/3/2017 6:06	51
14/3/2017 0:51	54	15/3/2017 1:56	53	16/3/2017 3:01	52	17/3/2017 4:06	51	18/3/2017 5:11	53	19/3/2017 6:16	53	20/3/2017 6:06	54	20/3/2017 6:11	51	20/3/2017 6:16	51
14/3/2017 0:56	54	15/3/2017 2:01	52	16/3/2017 3:06	54	17/3/2017 4:11	51	18/3/2017 5:16	54	19/3/2017 6:21	54	20/3/2017 6:16	54	20/3/2017 6:21	51	20/3/2017 6:26	51
14/3/2017 1:01	54	15/3/2017 2:06	52	16/3/2017 3:11	52	17/3/2017 4:16	51	18/3/2017 5:21	54	19/3/2017 6:26	54	20/3/2017 6:26	54	20/3/2017 6:31	51	20/3/2017 6:36	51
14/3/2017 1:06	54	15/3/2017 2:11	52	16/3/2017 3:16	52	17/3/2017 4:21	52	18/3/2017 5:26	53	19/3/2017 6:31	54	20/3/2017 6:36	54	20/3/2017 6:41	51	20/3/2017 6:46	51
14/3/2017 1:11	54	15/3/2017 2:16	53	16/3/2017 3:21	57	17/3/2017 4:26	51	18/3/2017 5:31	55	19/3/2017 6:36	55	20/3/2017 6:46	54	20/3/2017 6:51	51	20/3/2017 6:56	51
14/3/2017 1:16	54	15/3/2017 2:21	52	16/3/2017 3:26	54	17/3/2017 4:31	53	18/3/2017 5:36	55	19/3/2017 6:41	55	20/3/2017 6:56	54	20/3/2017 7:01	51	20/3/2017 7:06	51
14/3/2017 1:21	54	15/3/2017 2:26	52	16/3/2017 3:31	54	17/3/2017 4:36	51	18/3/2017 5:41	53	19/3/2017 6:46	55	20/3/2017 7:06	54	20/3/2017 7:11	51	20/3/2017 7:16	51
14/3/2017 1:26	54	15/3/2017 2:31	52	16/3/2017 3:36	52	17/3/2017 4:41	51	18/3/2017 5:46	53	19/3/2017 6:51	56	20/3/2017 7:16	54	20/3/2017 7:21	51	20/3/2017 7:26	51
14/3/2017 1:31	54	15/3/2017 2:36	52	16/3/2017 3:41	51	17/3/2017 4:46	51	18/3/2017 5:51	55	19/3/2017 6:56	55	20/3/2017 7:26	54	20/3/2017 7:31	51	20/3/2017 7:36	51
14/3/2017 1:36	56	15/3/2017 2:41	51	16/3/2017 3:46	52	17/3/2017 4:51	51	18/3/2017 5:56	55	19/3/2017 7:01	57	20/3/2017 7:36	54	20/3/2017 7:41	51	20/3/2017 7:46	51
14/3/2017 1:41	55	15/3/2017 2:46	52	16/3/2017 3:51	52	17/3/2017 4:56	53	18/3/2017 6:01	54	19/3/2017 7:06	55	20/3/2017 7:46	54	20/3/2017 7:51	51	20/3/2017 7:56	51
14/3/2017 1:46	54	15/3/2017 2:51	52	16/3/2017 3:56	52	17/3/2017 5:01	52	18/3/2017 6:06	53	19/3/2017 7:11	55	20/3/2017 7:56	54	20/3/2017 8:01	51	20/3/2017 8:06	51
14/3/2017 1:51	53	15/3/2017 2:56	55	16/3/2017 4:01	52	17/3/2017 5:06	51	18/3/2017 6:11	54	19/3/2017 7:16	55	20/3/2017 8:06	54	20/3/2017 8:11	51	20/3/2017 8:16	51
14/3/2017 1:56	53	15/3/2017 3:01	52	16/3/2017 4:06	52	17/3/2017 5:11	51	18/3/2017 6:16	54	19/3/2017 7:21	56	20/3/2017 8:16	54	20/3/2017 8:21	51	20/3/2017 8:26	51
14/3/2017 2:01	53	15/3/2017 3:06	54	16/3/2017 4:11	51	17/3/2017 5:16	52	18/3/2017 6:21	54	19/3/2017 7:26	56	20/3/2017 8:26	54	20/3/2017 8:31	51	20/3/2017 8:36	51
14/3/2017 2:06	53	15/3/2017 3:11	52	16/3/2017 4:16	52	17/3/2017 5:21	53	18/3/2017 6:26	54	19/3/2017 7:31	57	20/					

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
20/3/2017 4:26	50	21/3/2017 5:31	54	22/3/2017 6:36	55	23/3/2017 23:41	56	25/3/2017 0:46	55	26/3/2017 1:51	55
20/3/2017 4:31	50	21/3/2017 5:36	53	22/3/2017 6:41	55	23/3/2017 23:46	55	25/3/2017 0:51	55	26/3/2017 1:56	54
20/3/2017 4:36	52	21/3/2017 5:41	53	22/3/2017 6:46	55	23/3/2017 23:51	56	25/3/2017 0:56	55	26/3/2017 2:01	54
20/3/2017 4:41	52	21/3/2017 5:46	53	22/3/2017 6:51	55	23/3/2017 23:56	56	25/3/2017 1:01	56	26/3/2017 2:06	55
20/3/2017 4:46	53	21/3/2017 5:51	54	22/3/2017 6:56	55	24/3/2017 0:01	56	25/3/2017 1:06	55	26/3/2017 2:11	54
20/3/2017 4:51	51	21/3/2017 5:56	54	22/3/2017 23:01	56	24/3/2017 0:06	55	25/3/2017 1:11	58	26/3/2017 2:16	54
20/3/2017 4:56	51	21/3/2017 6:01	53	22/3/2017 23:06	55	24/3/2017 0:11	55	25/3/2017 1:16	56	26/3/2017 2:21	54
20/3/2017 5:01	51	21/3/2017 6:06	54	22/3/2017 23:11	55	24/3/2017 0:16	55	25/3/2017 1:21	55	26/3/2017 2:26	53
20/3/2017 5:06	51	21/3/2017 6:11	55	22/3/2017 23:16	57	24/3/2017 0:21	56	25/3/2017 1:26	54	26/3/2017 2:31	54
20/3/2017 5:11	52	21/3/2017 6:16	55	22/3/2017 23:21	56	24/3/2017 0:26	55	25/3/2017 1:31	54	26/3/2017 2:36	54
20/3/2017 5:16	52	21/3/2017 6:21	55	22/3/2017 23:26	56	24/3/2017 0:31	54	25/3/2017 1:36	54	26/3/2017 2:41	54
20/3/2017 5:21	53	21/3/2017 6:26	55	22/3/2017 23:31	56	24/3/2017 0:36	54	25/3/2017 1:41	56	26/3/2017 2:46	54
20/3/2017 5:26	52	21/3/2017 6:31	54	22/3/2017 23:36	56	24/3/2017 0:41	54	25/3/2017 1:46	57	26/3/2017 2:51	55
20/3/2017 5:31	52	21/3/2017 6:36	55	22/3/2017 23:41	55	24/3/2017 0:46	54	25/3/2017 1:51	54	26/3/2017 2:56	54
20/3/2017 5:36	53	21/3/2017 6:41	56	22/3/2017 23:46	55	24/3/2017 0:51	54	25/3/2017 1:56	56	26/3/2017 3:01	54
20/3/2017 5:41	53	21/3/2017 6:46	56	22/3/2017 23:51	55	24/3/2017 0:56	54	25/3/2017 2:01	54	26/3/2017 3:06	54
20/3/2017 5:46	53	21/3/2017 6:51	58	22/3/2017 23:56	56	24/3/2017 1:01	54	25/3/2017 2:06	55	26/3/2017 3:11	54
20/3/2017 5:51	55	21/3/2017 6:56	56	23/3/2017 0:01	56	24/3/2017 1:06	55	25/3/2017 2:11	53	26/3/2017 3:16	55
20/3/2017 5:56	53	21/3/2017 23:01	56	23/3/2017 0:06	55	24/3/2017 1:11	56	25/3/2017 2:16	55	26/3/2017 3:21	53
20/3/2017 6:01	53	21/3/2017 23:06	55	23/3/2017 0:11	55	24/3/2017 1:16	55	25/3/2017 2:21	54	26/3/2017 3:26	53
20/3/2017 6:06	53	21/3/2017 23:11	56	23/3/2017 0:16	54	24/3/2017 1:21	55	25/3/2017 2:26	54	26/3/2017 3:31	54
20/3/2017 6:11	53	21/3/2017 23:16	57	23/3/2017 0:21	55	24/3/2017 1:26	55	25/3/2017 2:31	54	26/3/2017 3:36	54
20/3/2017 6:16	54	21/3/2017 23:21	55	23/3/2017 0:26	55	24/3/2017 1:31	54	25/3/2017 2:36	50	26/3/2017 3:41	55
20/3/2017 6:21	54	21/3/2017 23:26	55	23/3/2017 0:31	54	24/3/2017 1:36	55	25/3/2017 2:41	54	26/3/2017 3:46	53
20/3/2017 6:26	55	21/3/2017 23:31	55	23/3/2017 0:36	54	24/3/2017 1:41	53	25/3/2017 2:46	55	26/3/2017 3:51	54
20/3/2017 6:31	55	21/3/2017 23:36	56	23/3/2017 0:41	54	24/3/2017 1:46	55	25/3/2017 2:51	54	26/3/2017 3:56	53
20/3/2017 6:36	55	21/3/2017 23:41	55	23/3/2017 0:46	54	24/3/2017 1:51	55	25/3/2017 2:56	54	26/3/2017 4:01	53
20/3/2017 6:41	56	21/3/2017 23:46	56	23/3/2017 0:51	54	24/3/2017 1:56	53	25/3/2017 3:01	53	26/3/2017 4:06	53
20/3/2017 6:46	55	21/3/2017 23:51	56	23/3/2017 0:56	55	24/3/2017 2:01	53	25/3/2017 3:06	55	26/3/2017 4:11	53
20/3/2017 6:51	56	21/3/2017 23:56	56	23/3/2017 1:01	54	24/3/2017 2:06	53	25/3/2017 3:11	54	26/3/2017 4:16	54
20/3/2017 6:56	55	22/3/2017 0:01	55	23/3/2017 1:06	54	24/3/2017 2:11	54	25/3/2017 3:16	53	26/3/2017 4:21	54
20/3/2017 23:01	58	22/3/2017 0:06	55	23/3/2017 1:11	54	24/3/2017 2:16	53	25/3/2017 3:21	53	26/3/2017 4:26	53
20/3/2017 23:06	56	22/3/2017 0:11	55	23/3/2017 1:16	55	24/3/2017 2:21	53	25/3/2017 3:26	53	26/3/2017 4:31	53
20/3/2017 23:11	49	22/3/2017 0:16	55	23/3/2017 1:21	54	24/3/2017 2:26	53	25/3/2017 3:31	53	26/3/2017 4:36	52
20/3/2017 23:16	57	22/3/2017 0:21	55	23/3/2017 1:26	54	24/3/2017 2:31	53	25/3/2017 3:36	53	26/3/2017 4:41	53
20/3/2017 23:21	56	22/3/2017 0:26	56	23/3/2017 1:31	54	24/3/2017 2:36	53	25/3/2017 3:41	53	26/3/2017 4:46	53
20/3/2017 23:26	57	22/3/2017 0:31	54	23/3/2017 1:36	54	24/3/2017 2:41	52	25/3/2017 3:46	53	26/3/2017 4:51	53
20/3/2017 23:31	56	22/3/2017 0:36	54	23/3/2017 1:41	55	24/3/2017 2:46	52	25/3/2017 3:51	53	26/3/2017 4:56	53
20/3/2017 23:36	55	22/3/2017 0:41	54	23/3/2017 1:46	53	24/3/2017 2:51	52	25/3/2017 3:56	53	26/3/2017 5:01	53
20/3/2017 23:41	56	22/3/2017 0:46	54	23/3/2017 1:51	54	24/3/2017 2:56	52	25/3/2017 4:01	53	26/3/2017 5:06	53
20/3/2017 23:46	56	22/3/2017 0:51	54	23/3/2017 1:56	53	24/3/2017 3:01	52	25/3/2017 4:06	52	26/3/2017 5:11	54
20/3/2017 23:51	57	22/3/2017 0:56	54	23/3/2017 2:01	53	24/3/2017 3:06	53	25/3/2017 4:11	53	26/3/2017 5:16	54
20/3/2017 23:56	56	22/3/2017 1:01	54	23/3/2017 2:06	53	24/3/2017 3:11	53	25/3/2017 4:16	53	26/3/2017 5:21	53
21/3/2017 0:01	56	22/3/2017 1:06	53	23/3/2017 2:11	53	24/3/2017 3:16	52	25/3/2017 4:21	52	26/3/2017 5:26	53
21/3/2017 0:06	56	22/3/2017 1:11	54	23/3/2017 2:16	53	24/3/2017 3:21	53	25/3/2017 4:26	52	26/3/2017 5:31	53
21/3/2017 0:11	55	22/3/2017 1:16	54	23/3/2017 2:21	53	24/3/2017 3:26	53	25/3/2017 4:31	53	26/3/2017 5:36	53
21/3/2017 0:16	56	22/3/2017 1:21	53	23/3/2017 2:26	52	24/3/2017 3:31	52	25/3/2017 4:36	52	26/3/2017 5:41	53
21/3/2017 0:21	56	22/3/2017 1:26	54	23/3/2017 2:31	53	24/3/2017 3:36	52	25/3/2017 4:41	54	26/3/2017 5:46	54
21/3/2017 0:26	55	22/3/2017 1:31	54	23/3/2017 2:36	53	24/3/2017 3:41	52	25/3/2017 4:46	53	26/3/2017 5:51	54
21/3/2017 0:31	56	22/3/2017 1:36	54	23/3/2017 2:41	53	24/3/2017 3:46	54	25/3/2017 4:51	54	26/3/2017 5:56	54
21/3/2017 0:36	55	22/3/2017 1:41	53	23/3/2017 2:46	54	24/3/2017 3:51	53	25/3/2017 4:56	54	26/3/2017 6:01	54
21/3/2017 0:41	55	22/3/2017 1:46	54	23/3/2017 2:51	53	24/3/2017 3:56	52	25/3/2017 5:01	55	26/3/2017 6:06	54
21/3/2017 0:46	58	22/3/2017 1:51	53	23/3/2017 2:56	53	24/3/2017 4:01	52	25/3/2017 5:06	55	26/3/2017 6:11	54
21/3/2017 0:51	57	22/3/2017 1:56	53	23/3/2017 3:01	53	24/3/2017 4:06	51	25/3/2017 5:11	54	26/3/2017 6:16	55
21/3/2017 0:56	55	22/3/2017 2:01	53	23/3/2017 3:06	53	24/3/2017 4:11	51	25/3/2017 5:16	54	26/3/2017 6:21	55
21/3/2017 1:01	56	22/3/2017 2:06	53	23/3/2017 3:11	53	24/3/2017 4:16	52	25/3/2017 5:21	55	26/3/2017 6:26	55
21/3/2017 1:06	56	22/3/2017 2:11	53	23/3/2017 3:16	53	24/3/2017 4:21	52	25/3/2017 5:26	56	26/3/2017 6:31	55
21/3/2017 1:11	55	22/3/2017 2:16	53	23/3/2017 3:21	52	24/3/2017 4:26	52	25/3/2017 5:31	56	26/3/2017 6:36	54
21/3/2017 1:16	55	22/3/2017 2:21	53	23/3/2017 3:26	52	24/3/2017 4:31	52	25/3/2017 5:36	54	26/3/2017 6:41	55
21/3/2017 1:21	55	22/3/2017 2:26	53	23/3/2017 3:31	52	24/3/2017 4:36	52	25/3/2017 5:41	55	26/3/2017 6:46	56
21/3/2017 1:26	55	22/3/2017 2:31	52	23/3/2017 3:36	52	24/3/2017 4:41	52	25/3/2017 5:46	54	26/3/2017 6:51	55
21/3/2017 1:31	53	22/3/2017 2:36	52	23/3/2017 3:41	52	24/3/2017 4:46	52	25/3/2017 5:51	55	26/3/2017 6:56	55
21/3/2017 1:36	54	22/3/2017 2:41	52	23/3/2017 3:46	52	24/3/2017 4:51	52	25/3/2017 5:56	55	26/3/2017 23:01	55
21/3/2017 1:41	56	22/3/2017 2:46	53	23/3/2017 3:51	53	24/3/2017 4:56	52	25/3/2017 6:01	56	26/3/2017 23:06	57
21/3/2017 1:46	54	22/3/2017 2:51	53	23/3/2017 3:56	52	24/3/2017 5:01	52	25/3/2017 6:06	55	26/3/2017 23:11	57
21/3/2017 1:51	54	22/3/2017 2:56	52	23/3/2017 4:01	52	24/3/2017 5:06	53	25/3/2017 6:11	55	26/3/2017 23:16	56
21/3/2017 1:56	54	22/3/2017 3:01	52	23/3/2017 4:06	52	24/3/2017 5:11	54	25/3/2017 6:16	55	26/3/2017 23:21	55
21/3/2017 2:01	54	22/3/2017 3:06	52	23/3/2017 4:11	52	24/3/2017 5:16	53	25/3/2017 6:21	55	26/3/2017 23:26	55
21/3/2017 2:06	55	22/3/2017 3:11	52	23/3/2017 4:16	52	24/3/2017 5:21	53	25/3/2017 6:26	55	26/3/2017 23:31	55
21/3/2017 2:11	53	22/3/2017 3:16	58	23/3/2017 4:21	52	24/3/2017 5:26	53	25/3/2017 6:31	55	26/3/2017 23:36	55
21/3/2017 2:16	53	22/3/2017 3:21	51	23/3/2017 4:26	52	24/3/2017 5:31	53	25/3/2017 6:36	56	26/3/2017 23:41	55
21/3/2017 2:21	56	22/3/2017 3:26	52	23/3/2017 4:31	51	24/3/2017 5:36	52	25/3/2017 6:41	55	26/3/2017 23:46	55
21/3/2017 2:26	53	22/3/2017 3:31	52	23/3/2017 4:36	51	24/3/2017 5:41	53	25/3/2017 6:46	56	26/3/2017 23:51	55
21/3/2017 2:31	54	22/3/2017 3:36	52	23/3/2017 4:41	52	24/3/2017 5:46	54	25/3/2017 6:51	53	26/3/2017 23:56	55
21/3/2017 2:36	53	22/3/2017 3:41	52	23/3/2017 4:46	52	24/3/2017 5:51	53	25/3/2017 6:56	58		
21/3/2017 2:41	52	22/3/2017 3:46	52	23/3/2017 4:51	52	24/3/2017 5:					

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
Normal Day 07:00-19:00											
27/2/2017 7:01	67	3/3/2017 13:01	67	9/3/2017 7:31	66	14/3/2017 14:01	68	20/3/2017 8:31	67	24/3/2017 15:01	64
27/2/2017 7:31	67	3/3/2017 13:31	68	9/3/2017 8:01	65	14/3/2017 14:31	69	20/3/2017 9:01	67	24/3/2017 15:31	64
27/2/2017 8:01	66	3/3/2017 14:01	68	9/3/2017 8:31	65	14/3/2017 15:01	69	20/3/2017 9:31	68	24/3/2017 16:01	64
27/2/2017 8:31	66	3/3/2017 14:31	67	9/3/2017 9:01	65	14/3/2017 15:31	69	20/3/2017 10:01	69	24/3/2017 16:31	64
27/2/2017 9:01	67	3/3/2017 15:01	68	9/3/2017 9:31	66	14/3/2017 16:01	68	20/3/2017 10:31	68	24/3/2017 17:01	64
27/2/2017 9:31	69	3/3/2017 15:31	67	9/3/2017 10:01	67	14/3/2017 16:31	68	20/3/2017 11:01	68	24/3/2017 17:31	65
27/2/2017 10:01	70	3/3/2017 16:01	67	9/3/2017 10:31	68	14/3/2017 17:01	67	20/3/2017 11:31	65	24/3/2017 18:01	66
27/2/2017 10:31	57	3/3/2017 16:31	67	9/3/2017 11:01	68	14/3/2017 17:31	66	20/3/2017 12:01	64	24/3/2017 18:31	66
27/2/2017 11:01	59	3/3/2017 17:01	66	9/3/2017 11:31	67	14/3/2017 18:01	66	20/3/2017 12:31	66	25/3/2017 7:01	65
27/2/2017 11:31	59	3/3/2017 17:31	67	9/3/2017 12:01	66	14/3/2017 18:31	66	20/3/2017 13:01	67	25/3/2017 7:31	66
27/2/2017 12:01	67	3/3/2017 18:01	67	9/3/2017 12:31	66	15/3/2017 7:01	67	20/3/2017 13:31	67	25/3/2017 8:01	67
27/2/2017 12:31	67	3/3/2017 18:31	67	9/3/2017 13:01	68	15/3/2017 7:31	67	20/3/2017 14:01	67	25/3/2017 8:31	67
27/2/2017 13:01	67	4/3/2017 7:01	65	9/3/2017 13:31	68	15/3/2017 8:01	66	20/3/2017 14:31	68	25/3/2017 9:01	67
27/2/2017 13:31	68	4/3/2017 7:31	65	9/3/2017 14:01	68	15/3/2017 8:31	66	20/3/2017 15:01	68	25/3/2017 9:31	67
27/2/2017 14:01	68	4/3/2017 8:01	64	9/3/2017 14:31	67	15/3/2017 9:01	68	20/3/2017 15:31	68	25/3/2017 10:01	67
27/2/2017 14:31	69	4/3/2017 8:31	68	9/3/2017 15:01	67	15/3/2017 9:31	67	20/3/2017 16:01	69	25/3/2017 10:31	67
27/2/2017 15:01	69	4/3/2017 9:01	67	9/3/2017 15:31	68	15/3/2017 10:01	68	20/3/2017 16:31	68	25/3/2017 11:01	65
27/2/2017 15:31	68	4/3/2017 9:31	68	9/3/2017 16:01	68	15/3/2017 10:31	66	20/3/2017 17:01	67	25/3/2017 11:31	67
27/2/2017 16:01	68	4/3/2017 10:01	67	9/3/2017 16:31	68	15/3/2017 11:01	67	20/3/2017 17:31	66	25/3/2017 12:01	64
27/2/2017 16:31	68	4/3/2017 10:31	67	9/3/2017 17:01	68	15/3/2017 11:31	67	20/3/2017 18:01	66	25/3/2017 12:31	65
27/2/2017 17:01	67	4/3/2017 11:01	66	9/3/2017 17:31	66	15/3/2017 12:01	67	20/3/2017 18:31	65	25/3/2017 13:01	68
27/2/2017 17:31	66	4/3/2017 11:31	66	9/3/2017 18:01	66	15/3/2017 12:31	67	21/3/2017 7:01	66	25/3/2017 13:31	67
27/2/2017 18:01	67	4/3/2017 12:01	66	9/3/2017 18:31	66	15/3/2017 13:01	68	21/3/2017 7:31	65	25/3/2017 14:01	67
27/2/2017 18:31	66	4/3/2017 12:31	66	10/3/2017 7:01	66	15/3/2017 13:31	67	21/3/2017 8:01	65	25/3/2017 14:31	66
28/2/2017 7:01	66	4/3/2017 13:01	65	10/3/2017 7:31	66	15/3/2017 14:01	67	21/3/2017 8:31	67	25/3/2017 15:01	66
28/2/2017 7:31	67	4/3/2017 13:31	65	10/3/2017 8:01	63	15/3/2017 14:31	67	21/3/2017 9:01	67	25/3/2017 15:31	66
28/2/2017 8:01	66	4/3/2017 14:01	66	10/3/2017 8:31	66	15/3/2017 15:01	67	21/3/2017 9:31	68	25/3/2017 16:01	67
28/2/2017 8:31	67	4/3/2017 14:31	67	10/3/2017 9:01	66	15/3/2017 15:31	67	21/3/2017 10:01	68	25/3/2017 16:31	67
28/2/2017 9:01	68	4/3/2017 15:01	66	10/3/2017 9:31	67	15/3/2017 16:01	67	21/3/2017 10:31	68	25/3/2017 17:01	66
28/2/2017 9:31	68	4/3/2017 15:31	66	10/3/2017 10:01	67	15/3/2017 16:31	68	21/3/2017 11:01	69	25/3/2017 17:31	66
28/2/2017 10:01	68	4/3/2017 16:01	67	10/3/2017 10:31	68	15/3/2017 17:01	67	21/3/2017 11:31	67	25/3/2017 18:01	66
28/2/2017 10:31	68	4/3/2017 16:31	67	10/3/2017 11:01	68	15/3/2017 17:31	67	21/3/2017 12:01	66	25/3/2017 18:31	65
28/2/2017 11:01	67	4/3/2017 17:01	66	10/3/2017 11:31	67	15/3/2017 18:01	66	21/3/2017 12:31	67		
28/2/2017 11:31	67	4/3/2017 17:31	66	10/3/2017 12:01	66	15/3/2017 18:31	66	21/3/2017 13:01	68	Normal Day 19:00-23:00 Sunday & Holiday 07:00-23:00	
28/2/2017 12:01	67	4/3/2017 18:01	66	10/3/2017 12:31	66	16/3/2017 7:01	67	21/3/2017 13:31	69		
28/2/2017 12:31	67	4/3/2017 18:31	66	10/3/2017 13:01	67	16/3/2017 7:31	66	21/3/2017 14:01	68	27/2/2017 19:01	54
28/2/2017 13:01	67	6/3/2017 7:01	66	10/3/2017 13:31	67	16/3/2017 8:01	67	21/3/2017 14:31	69	27/2/2017 19:06	66
28/2/2017 13:31	67	6/3/2017 7:31	66	10/3/2017 14:01	67	16/3/2017 8:31	67	21/3/2017 15:01	68	27/2/2017 19:11	66
28/2/2017 14:01	68	6/3/2017 8:01	66	10/3/2017 14:31	67	16/3/2017 9:01	68	21/3/2017 15:31	67	27/2/2017 19:16	66
28/2/2017 14:31	67	6/3/2017 8:31	64	10/3/2017 15:01	67	16/3/2017 9:31	68	21/3/2017 16:01	68	27/2/2017 19:21	66
28/2/2017 15:01	67	6/3/2017 9:01	66	10/3/2017 15:31	67	16/3/2017 10:01	67	21/3/2017 16:31	69	27/2/2017 19:26	66
28/2/2017 15:31	69	6/3/2017 9:31	67	10/3/2017 16:01	67	16/3/2017 10:31	67	21/3/2017 17:01	66	27/2/2017 19:31	66
28/2/2017 16:01	68	6/3/2017 10:01	67	10/3/2017 16:31	67	16/3/2017 11:01	69	21/3/2017 17:31	66	27/2/2017 19:36	66
28/2/2017 16:31	68	6/3/2017 10:31	67	10/3/2017 17:01	66	16/3/2017 11:31	68	21/3/2017 18:01	67	27/2/2017 19:41	66
28/2/2017 17:01	68	6/3/2017 11:01	67	10/3/2017 17:31	66	16/3/2017 12:01	66	21/3/2017 18:31	66	27/2/2017 19:46	66
28/2/2017 17:31	67	6/3/2017 11:31	66	10/3/2017 18:01	66	16/3/2017 12:31	68	22/3/2017 7:01	66	27/2/2017 19:51	66
28/2/2017 18:01	66	6/3/2017 12:01	66	10/3/2017 18:31	62	16/3/2017 13:01	67	22/3/2017 7:31	64	27/2/2017 19:56	66
28/2/2017 18:31	66	6/3/2017 12:31	66	11/3/2017 7:01	65	16/3/2017 13:31	67	22/3/2017 8:01	64	27/2/2017 20:01	65
1/3/2017 7:01	66	6/3/2017 13:01	66	11/3/2017 7:31	66	16/3/2017 14:01	66	22/3/2017 8:31	67	27/2/2017 20:06	66
1/3/2017 7:31	65	6/3/2017 13:31	66	11/3/2017 8:01	66	16/3/2017 14:31	67	22/3/2017 9:01	67	27/2/2017 20:11	65
1/3/2017 8:01	65	6/3/2017 14:01	67	11/3/2017 8:31	67	16/3/2017 15:01	67	22/3/2017 9:31	65	27/2/2017 20:16	66
1/3/2017 8:31	64	6/3/2017 14:31	67	11/3/2017 9:01	67	16/3/2017 15:31	67	22/3/2017 10:01	64	27/2/2017 20:21	66
1/3/2017 9:01	66	6/3/2017 15:01	66	11/3/2017 9:31	67	16/3/2017 16:01	67	22/3/2017 10:31	66	27/2/2017 20:26	65
1/3/2017 9:31	66	6/3/2017 15:31	67	11/3/2017 10:01	66	16/3/2017 16:31	67	22/3/2017 11:01	66	27/2/2017 20:31	65
1/3/2017 10:01	67	6/3/2017 16:01	67	11/3/2017 10:31	66	16/3/2017 17:01	65	22/3/2017 11:31	64	27/2/2017 20:36	66
1/3/2017 10:31	67	6/3/2017 16:31	67	11/3/2017 11:01	67	16/3/2017 17:31	67	22/3/2017 12:01	66	27/2/2017 20:41	65
1/3/2017 11:01	67	6/3/2017 17:01	66	11/3/2017 11:31	66	16/3/2017 18:01	67	22/3/2017 12:31	65	27/2/2017 20:46	66
1/3/2017 11:31	65	6/3/2017 17:31	66	11/3/2017 12:01	65	16/3/2017 18:31	66	22/3/2017 13:01	65	27/2/2017 20:51	66
1/3/2017 12:01	65	6/3/2017 18:01	66	11/3/2017 12:31	66	16/3/2017 19:01	66	22/3/2017 13:31	68	27/2/2017 20:56	65
1/3/2017 12:31	66	6/3/2017 18:31	66	11/3/2017 13:01	66	16/3/2017 19:31	65	22/3/2017 14:01	68	27/2/2017 21:01	65
1/3/2017 13:01	66	7/3/2017 7:01	66	11/3/2017 13:31	66	16/3/2017 20:01	66	22/3/2017 14:31	67	27/2/2017 21:06	66
1/3/2017 13:31	66	7/3/2017 7:31	66	11/3/2017 14:01	66	16/3/2017 20:31	65	22/3/2017 15:01	65	27/2/2017 21:11	65
1/3/2017 14:01	67	7/3/2017 8:01	66	11/3/2017 14:31	66	16/3/2017 21:01	67	22/3/2017 15:31	65	27/2/2017 21:16	65
1/3/2017 14:31	67	7/3/2017 8:31	66	11/3/2017 15:01	66	16/3/2017 21:31	68	22/3/2017 16:01	67	27/2/2017 21:21	65
1/3/2017 15:01	68	7/3/2017 9:01	66	11/3/2017 15:31	67	16/3/2017 22:01	66	22/3/2017 16:31	66	27/2/2017 21:26	65
1/3/2017 15:31	68	7/3/2017 9:31	68	11/3/2017 16:01	67	16/3/2017 22:31	67	22/3/2017 17:01	67	27/2/2017 21:31	65
1/3/2017 16:01	68	7/3/2017 10:01	68	11/3/2017 16:31	68	16/3/2017 23:01	66	22/3/2017 17:31	66	27/2/2017 21:36	65
1/3/2017 16:31	66	7/3/2017 10:31	69	11/3/2017 17:01	67	16/3/2017 23:31	65	22/3/2017 18:01	66	27/2/2017 21:41	64
1/3/2017 17:01	67	7/3/2017 11:01	68	11/3/2017 17:31	67	16/3/2017 24:01	66	22/3/2017 18:31	66	27/2/2017 21:46	65
1/3/2017 17:31	66	7/3/2017 11:31	67	11/3/2017 18:01	66	16/3/2017 24:31	67	22/3/2017 19:01	67	27/2/2017 21:51	65
1/3/2017 18:01	67	7/3/2017 12:01	66	11/3/2017 18:31	65	16/3/2017 25:01	66	22/3/2017 19:31	68	27/2/2017 21:56	65
1/3/2017 18:31	66	7/3/2017 12:31	67	11/3/2017 19:01	66	16/3/2017 25:31	66	22/3/2017 20:01	67	27/2/2017 22:01	65
2/3/2017 7:01	67	7/3/2017 13:01	68	11/3/2017 19:31	67	16/3/2017 26:01	66	22/3/2017 20:31	68	27/2/2017 22:06	65
2/3/2017 7:31	67	7/3/2017 13:31	68	11/3/2017 20:01	66	16/3/2017 26:31	66	22/3/2017 21:01	67	27/2/2017 22:	

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
28/2/2017 21:01	65	2/3/2017 22:06	65	5/3/2017 7:11	64	5/3/2017 16:16	65	6/3/2017 21:21	65	8/3/2017 22:26	65
28/2/2017 21:06	66	2/3/2017 22:11	64	5/3/2017 7:16	65	5/3/2017 16:21	65	6/3/2017 21:26	64	8/3/2017 22:31	64
28/2/2017 21:11	65	2/3/2017 22:16	65	5/3/2017 7:21	65	5/3/2017 16:26	66	6/3/2017 21:31	64	8/3/2017 22:36	64
28/2/2017 21:16	65	2/3/2017 22:21	65	5/3/2017 7:26	66	5/3/2017 16:31	65	6/3/2017 21:36	64	8/3/2017 22:41	64
28/2/2017 21:21	65	2/3/2017 22:26	65	5/3/2017 7:31	64	5/3/2017 16:36	65	6/3/2017 21:41	65	8/3/2017 22:46	64
28/2/2017 21:26	65	2/3/2017 22:31	66	5/3/2017 7:36	66	5/3/2017 16:41	65	6/3/2017 21:46	64	8/3/2017 22:51	65
28/2/2017 21:31	65	2/3/2017 22:36	65	5/3/2017 7:41	66	5/3/2017 16:46	65	6/3/2017 21:51	64	8/3/2017 22:56	64
28/2/2017 21:36	65	2/3/2017 22:41	65	5/3/2017 7:46	66	5/3/2017 16:51	66	6/3/2017 21:56	65	9/3/2017 19:01	66
28/2/2017 21:41	43	2/3/2017 22:46	65	5/3/2017 7:51	65	5/3/2017 16:56	65	6/3/2017 22:01	65	9/3/2017 19:06	66
28/2/2017 21:46	65	2/3/2017 22:51	64	5/3/2017 7:56	66	5/3/2017 17:01	65	6/3/2017 22:06	65	9/3/2017 19:11	66
28/2/2017 21:51	65	2/3/2017 22:56	65	5/3/2017 8:01	66	5/3/2017 17:06	65	6/3/2017 22:11	64	9/3/2017 19:16	66
28/2/2017 21:56	66	3/3/2017 19:01	57	5/3/2017 8:06	65	5/3/2017 17:11	65	6/3/2017 22:16	65	9/3/2017 19:21	53
28/2/2017 22:01	66	3/3/2017 19:06	53	5/3/2017 8:11	65	5/3/2017 17:16	65	6/3/2017 22:21	65	9/3/2017 19:26	66
28/2/2017 22:06	65	3/3/2017 19:11	61	5/3/2017 8:16	65	5/3/2017 17:21	66	6/3/2017 22:26	65	9/3/2017 19:31	57
28/2/2017 22:11	65	3/3/2017 19:16	66	5/3/2017 8:21	65	5/3/2017 17:26	65	6/3/2017 22:31	64	9/3/2017 19:36	66
28/2/2017 22:16	65	3/3/2017 19:21	55	5/3/2017 8:26	65	5/3/2017 17:31	65	6/3/2017 22:36	64	9/3/2017 19:41	66
28/2/2017 22:21	66	3/3/2017 19:26	66	5/3/2017 8:31	66	5/3/2017 17:36	65	6/3/2017 22:41	64	9/3/2017 19:46	66
28/2/2017 22:26	66	3/3/2017 19:31	66	5/3/2017 8:36	66	5/3/2017 17:41	66	6/3/2017 22:46	65	9/3/2017 19:51	66
28/2/2017 22:31	65	3/3/2017 19:36	66	5/3/2017 8:41	65	5/3/2017 17:46	66	6/3/2017 22:51	64	9/3/2017 19:56	66
28/2/2017 22:36	65	3/3/2017 19:41	66	5/3/2017 8:46	65	5/3/2017 17:51	65	6/3/2017 22:56	65	9/3/2017 20:01	66
28/2/2017 22:41	65	3/3/2017 19:46	66	5/3/2017 8:51	66	5/3/2017 17:56	65	7/3/2017 19:01	66	9/3/2017 20:06	66
28/2/2017 22:46	65	3/3/2017 19:51	66	5/3/2017 8:56	66	5/3/2017 18:01	66	7/3/2017 19:06	66	9/3/2017 20:11	66
28/2/2017 22:51	65	3/3/2017 19:56	66	5/3/2017 9:01	65	5/3/2017 18:06	65	7/3/2017 19:11	65	9/3/2017 20:16	66
28/2/2017 22:56	65	3/3/2017 20:01	65	5/3/2017 9:06	65	5/3/2017 18:11	65	7/3/2017 19:16	66	9/3/2017 20:21	65
1/3/2017 19:01	65	3/3/2017 20:06	66	5/3/2017 9:11	65	5/3/2017 18:16	66	7/3/2017 19:21	66	9/3/2017 20:26	65
1/3/2017 19:06	66	3/3/2017 20:11	66	5/3/2017 9:16	65	5/3/2017 18:21	65	7/3/2017 19:26	66	9/3/2017 20:31	65
1/3/2017 19:11	66	3/3/2017 20:16	66	5/3/2017 9:21	65	5/3/2017 18:26	66	7/3/2017 19:31	66	9/3/2017 20:36	66
1/3/2017 19:16	65	3/3/2017 20:21	65	5/3/2017 9:26	66	5/3/2017 18:31	66	7/3/2017 19:36	66	9/3/2017 20:41	63
1/3/2017 19:21	65	3/3/2017 20:26	49	5/3/2017 9:31	66	5/3/2017 18:36	66	7/3/2017 19:41	63	9/3/2017 20:46	65
1/3/2017 19:26	65	3/3/2017 20:31	65	5/3/2017 9:36	65	5/3/2017 18:41	66	7/3/2017 19:46	66	9/3/2017 20:51	65
1/3/2017 19:31	66	3/3/2017 20:36	64	5/3/2017 9:41	66	5/3/2017 18:46	66	7/3/2017 19:51	65	9/3/2017 20:56	65
1/3/2017 19:36	66	3/3/2017 20:41	65	5/3/2017 9:46	66	5/3/2017 18:51	65	7/3/2017 19:56	66	9/3/2017 21:01	64
1/3/2017 19:41	66	3/3/2017 20:46	66	5/3/2017 9:51	66	5/3/2017 18:56	65	7/3/2017 20:01	66	9/3/2017 21:06	64
1/3/2017 19:46	66	3/3/2017 20:51	65	5/3/2017 9:56	66	5/3/2017 19:01	66	7/3/2017 20:06	66	9/3/2017 21:11	65
1/3/2017 19:51	65	3/3/2017 20:56	65	5/3/2017 10:01	65	5/3/2017 19:06	65	7/3/2017 20:11	66	9/3/2017 21:16	65
1/3/2017 19:56	66	3/3/2017 21:01	65	5/3/2017 10:06	61	5/3/2017 19:11	65	7/3/2017 20:16	65	9/3/2017 21:21	64
1/3/2017 20:01	65	3/3/2017 21:06	66	5/3/2017 10:11	66	5/3/2017 19:16	65	7/3/2017 20:21	65	9/3/2017 21:26	64
1/3/2017 20:06	65	3/3/2017 21:11	65	5/3/2017 10:16	66	5/3/2017 19:21	65	7/3/2017 20:26	65	9/3/2017 21:31	64
1/3/2017 20:11	65	3/3/2017 21:16	66	5/3/2017 10:21	43	5/3/2017 19:26	66	7/3/2017 20:31	65	9/3/2017 21:36	64
1/3/2017 20:16	65	3/3/2017 21:21	66	5/3/2017 10:26	66	5/3/2017 19:31	66	7/3/2017 20:36	65	9/3/2017 21:41	65
1/3/2017 20:21	65	3/3/2017 21:26	65	5/3/2017 10:31	66	5/3/2017 19:36	65	7/3/2017 20:41	66	9/3/2017 21:46	65
1/3/2017 20:26	65	3/3/2017 21:31	65	5/3/2017 10:36	65	5/3/2017 19:41	65	7/3/2017 20:46	65	9/3/2017 21:51	65
1/3/2017 20:31	65	3/3/2017 21:36	65	5/3/2017 10:41	66	5/3/2017 19:46	64	7/3/2017 20:51	65	9/3/2017 21:56	64
1/3/2017 20:36	65	3/3/2017 21:41	65	5/3/2017 10:46	65	5/3/2017 19:51	64	7/3/2017 20:56	65	9/3/2017 22:01	64
1/3/2017 20:41	65	3/3/2017 21:46	65	5/3/2017 10:51	66	5/3/2017 19:56	65	7/3/2017 21:01	65	9/3/2017 22:06	65
1/3/2017 20:46	65	3/3/2017 21:51	65	5/3/2017 10:56	66	5/3/2017 20:01	64	7/3/2017 21:06	65	9/3/2017 22:11	64
1/3/2017 20:51	65	3/3/2017 21:56	65	5/3/2017 11:01	65	5/3/2017 20:06	65	7/3/2017 21:11	65	9/3/2017 22:16	65
1/3/2017 20:56	66	3/3/2017 22:01	65	5/3/2017 11:06	65	5/3/2017 20:11	65	7/3/2017 21:16	65	9/3/2017 22:21	65
1/3/2017 21:01	65	3/3/2017 22:06	65	5/3/2017 11:11	66	5/3/2017 20:16	65	7/3/2017 21:21	65	9/3/2017 22:26	65
1/3/2017 21:06	64	3/3/2017 22:11	65	5/3/2017 11:16	66	5/3/2017 20:21	64	7/3/2017 21:26	65	9/3/2017 22:31	65
1/3/2017 21:11	64	3/3/2017 22:16	66	5/3/2017 11:21	66	5/3/2017 20:26	64	7/3/2017 21:31	65	9/3/2017 22:36	65
1/3/2017 21:16	65	3/3/2017 22:21	65	5/3/2017 11:26	65	5/3/2017 20:31	65	7/3/2017 21:36	65	9/3/2017 22:41	64
1/3/2017 21:21	65	3/3/2017 22:26	65	5/3/2017 11:31	48	5/3/2017 20:36	65	7/3/2017 21:41	65	9/3/2017 22:46	64
1/3/2017 21:26	65	3/3/2017 22:31	66	5/3/2017 11:36	65	5/3/2017 20:41	64	7/3/2017 21:46	65	9/3/2017 22:51	65
1/3/2017 21:31	64	3/3/2017 22:36	65	5/3/2017 11:41	65	5/3/2017 20:46	64	7/3/2017 21:51	65	9/3/2017 22:56	65
1/3/2017 21:36	66	3/3/2017 22:41	65	5/3/2017 11:46	66	5/3/2017 20:51	64	7/3/2017 21:56	65	10/3/2017 19:01	64
1/3/2017 21:41	66	3/3/2017 22:46	66	5/3/2017 11:51	56	5/3/2017 20:56	64	7/3/2017 22:01	65	10/3/2017 19:06	65
1/3/2017 21:46	65	3/3/2017 22:51	66	5/3/2017 11:56	66	5/3/2017 21:01	64	7/3/2017 22:06	65	10/3/2017 19:11	65
1/3/2017 21:51	65	3/3/2017 22:56	66	5/3/2017 12:01	66	5/3/2017 21:06	65	7/3/2017 22:11	65	10/3/2017 19:16	66
1/3/2017 21:56	65	4/3/2017 19:01	65	5/3/2017 12:06	66	5/3/2017 21:11	66	7/3/2017 22:16	65	10/3/2017 19:21	66
1/3/2017 22:01	65	4/3/2017 19:06	66	5/3/2017 12:11	66	5/3/2017 21:16	64	7/3/2017 22:21	65	10/3/2017 19:26	65
1/3/2017 22:06	65	4/3/2017 19:11	65	5/3/2017 12:16	66	5/3/2017 21:21	64	7/3/2017 22:26	66	10/3/2017 19:31	66
1/3/2017 22:11	65	4/3/2017 19:16	66	5/3/2017 12:21	65	5/3/2017 21:26	64	7/3/2017 22:31	65	10/3/2017 19:36	65
1/3/2017 22:16	66	4/3/2017 19:21	66	5/3/2017 12:26	66	5/3/2017 21:31	65	7/3/2017 22:36	66	10/3/2017 19:41	66
1/3/2017 22:21	65	4/3/2017 19:26	65	5/3/2017 12:31	66	5/3/2017 21:36	65	7/3/2017 22:41	66	10/3/2017 19:46	66
1/3/2017 22:26	65	4/3/2017 19:31	65	5/3/2017 12:36	66	5/3/2017 21:41	64	7/3/2017 22:46	66	10/3/2017 19:51	66
1/3/2017 22:31	65	4/3/2017 19:36	65	5/3/2017 12:41	66	5/3/2017 21:46	65	7/3/2017 22:51	66	10/3/2017 19:56	66
1/3/2017 22:36	66	4/3/2017 19:41	66	5/3/2017 12:46	66	5/3/2017 21:51	64	7/3/2017 22:56	65	10/3/2017 20:01	65
1/3/2017 22:41	65	4/3/2017 19:46	65	5/3/2017 12:51	66	5/3/2017 21:56	65	8/3/2017 19:01	66	10/3/2017 20:06	65
1/3/2017 22:46	65	4/3/2017 19:51	65	5/3/2017 12:56	66	5/3/2017 22:01	64	8/3/2017 19:06	57	10/3/2017 20:11	66
1/3/2017 22:51	64	4/3/2017 19:56	65	5/3/2017 13:01	66	5/3/2017 22:06	64	8/3/2017 19:11	66	10/3/2017 20:16	66
1/3/2017 22:56	65	4/3/2017 20:01	66	5/3/2017 13:06	66	5/3/2017 22:11	64	8/3/2017 19:16	66	10/3/2017 20:21	45
2/3/2017 19:01	66	4/3/2017 20:06	65	5/3/2017 13:11	65	5/3/2017 22:16	64	8/3/2017 19:21	66	10/3/2017 20:26	65
2/3/2017 19:06	66	4/3/2017 20:11	64	5/3/2017 13:16	66	5/3/2017 22:21	65	8/3/2017 19:26	66	10/3/2017 20:31	65
2/3/2017 19:11	65	4/3/2017 20:16	65	5/3/2017 13:21	65	5/3/2017 22:26	64	8/3/2017 19:31	66	10/3/2017 20:36	65
2/3/2017 19:16	66	4/3/2017 20:21	65	5/3/2017 13:26	65	5/3/2017 22:31	64	8/3/2017 19:36	64	10	

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
11/3/2017 19:31	56	12/3/2017 12:36	66	12/3/2017 21:41	65	14/3/2017 22:46	65	17/3/2017 19:51	66	19/3/2017 8:56	66
11/3/2017 19:36	65	12/3/2017 12:41	66	12/3/2017 21:46	65	14/3/2017 22:51	65	17/3/2017 19:56	53	19/3/2017 9:01	66
11/3/2017 19:41	65	12/3/2017 12:46	66	12/3/2017 21:51	65	14/3/2017 22:56	65	17/3/2017 20:01	66	19/3/2017 9:06	66
11/3/2017 19:46	65	12/3/2017 12:51	66	12/3/2017 21:56	65	15/3/2017 19:01	66	17/3/2017 20:06	66	19/3/2017 9:11	66
11/3/2017 19:51	66	12/3/2017 12:56	66	12/3/2017 22:01	65	15/3/2017 19:06	51	17/3/2017 20:11	66	19/3/2017 9:16	66
11/3/2017 19:56	65	12/3/2017 13:01	66	12/3/2017 22:06	65	15/3/2017 19:11	66	17/3/2017 20:16	48	19/3/2017 9:21	66
11/3/2017 20:01	65	12/3/2017 13:06	66	12/3/2017 22:11	65	15/3/2017 19:16	65	17/3/2017 20:21	66	19/3/2017 9:26	53
11/3/2017 20:06	65	12/3/2017 13:11	66	12/3/2017 22:16	65	15/3/2017 19:21	46	17/3/2017 20:26	65	19/3/2017 9:31	66
11/3/2017 20:11	65	12/3/2017 13:16	66	12/3/2017 22:21	65	15/3/2017 19:26	66	17/3/2017 20:31	65	19/3/2017 9:36	65
11/3/2017 20:16	65	12/3/2017 13:21	66	12/3/2017 22:26	64	15/3/2017 19:31	56	17/3/2017 20:36	66	19/3/2017 9:41	65
11/3/2017 20:21	65	12/3/2017 13:26	66	12/3/2017 22:31	65	15/3/2017 19:36	47	17/3/2017 20:41	65	19/3/2017 9:46	65
11/3/2017 20:26	65	12/3/2017 13:31	66	12/3/2017 22:36	65	15/3/2017 19:41	66	17/3/2017 20:46	65	19/3/2017 9:51	65
11/3/2017 20:31	65	12/3/2017 13:36	66	12/3/2017 22:41	64	15/3/2017 19:46	55	17/3/2017 20:51	66	19/3/2017 9:56	65
11/3/2017 20:36	45	12/3/2017 13:41	66	12/3/2017 22:46	64	15/3/2017 19:51	66	17/3/2017 20:56	65	19/3/2017 10:01	65
11/3/2017 20:41	64	12/3/2017 13:46	56	12/3/2017 22:51	64	15/3/2017 19:56	66	17/3/2017 21:01	59	19/3/2017 10:06	66
11/3/2017 20:46	65	12/3/2017 13:51	66	12/3/2017 22:56	64	15/3/2017 20:01	55	17/3/2017 21:06	65	19/3/2017 10:11	65
11/3/2017 20:51	65	12/3/2017 13:56	66	13/3/2017 19:01	66	15/3/2017 20:06	65	17/3/2017 21:11	65	19/3/2017 10:16	65
11/3/2017 20:56	65	12/3/2017 14:01	43	13/3/2017 19:06	66	15/3/2017 20:11	67	17/3/2017 21:16	65	19/3/2017 10:21	66
11/3/2017 21:01	65	12/3/2017 14:06	46	13/3/2017 19:11	66	15/3/2017 20:16	66	17/3/2017 21:21	66	19/3/2017 10:26	66
11/3/2017 21:06	65	12/3/2017 14:11	55	13/3/2017 19:16	66	15/3/2017 20:21	65	17/3/2017 21:26	65	19/3/2017 10:31	65
11/3/2017 21:11	65	12/3/2017 14:16	56	13/3/2017 19:21	52	15/3/2017 20:26	66	17/3/2017 21:31	66	19/3/2017 10:36	65
11/3/2017 21:16	66	12/3/2017 14:21	49	13/3/2017 19:26	66	15/3/2017 20:31	66	17/3/2017 21:36	65	19/3/2017 10:41	65
11/3/2017 21:21	66	12/3/2017 14:26	58	13/3/2017 19:31	66	15/3/2017 20:36	65	17/3/2017 21:41	65	19/3/2017 10:46	65
11/3/2017 21:26	65	12/3/2017 14:31	55	13/3/2017 19:36	66	15/3/2017 20:41	65	17/3/2017 21:46	65	19/3/2017 10:51	65
11/3/2017 21:31	65	12/3/2017 14:36	66	13/3/2017 19:41	66	15/3/2017 20:46	65	17/3/2017 21:51	65	19/3/2017 10:56	65
11/3/2017 21:36	64	12/3/2017 14:41	66	13/3/2017 19:46	65	15/3/2017 20:51	65	17/3/2017 21:56	65	19/3/2017 11:01	65
11/3/2017 21:41	65	12/3/2017 14:46	66	13/3/2017 19:51	66	15/3/2017 20:56	65	17/3/2017 22:01	66	19/3/2017 11:06	65
11/3/2017 21:46	65	12/3/2017 14:51	66	13/3/2017 19:56	66	15/3/2017 21:01	65	17/3/2017 22:06	65	19/3/2017 11:11	65
11/3/2017 21:51	65	12/3/2017 14:56	66	13/3/2017 20:01	65	15/3/2017 21:06	65	17/3/2017 22:11	65	19/3/2017 11:16	66
11/3/2017 21:56	65	12/3/2017 15:01	56	13/3/2017 20:06	66	15/3/2017 21:11	65	17/3/2017 22:16	65	19/3/2017 11:21	65
11/3/2017 22:01	65	12/3/2017 15:06	66	13/3/2017 20:11	65	15/3/2017 21:16	65	17/3/2017 22:21	65	19/3/2017 11:26	65
11/3/2017 22:06	65	12/3/2017 15:11	59	13/3/2017 20:16	66	15/3/2017 21:21	65	17/3/2017 22:26	66	19/3/2017 11:31	66
11/3/2017 22:11	65	12/3/2017 15:16	54	13/3/2017 20:21	65	15/3/2017 21:26	66	17/3/2017 22:31	65	19/3/2017 11:36	66
11/3/2017 22:16	65	12/3/2017 15:21	57	13/3/2017 20:26	65	15/3/2017 21:31	65	17/3/2017 22:36	66	19/3/2017 11:41	66
11/3/2017 22:21	65	12/3/2017 15:26	47	13/3/2017 20:31	66	15/3/2017 21:36	65	17/3/2017 22:41	66	19/3/2017 11:46	66
11/3/2017 22:26	65	12/3/2017 15:31	64	13/3/2017 20:36	65	15/3/2017 21:41	65	17/3/2017 22:46	65	19/3/2017 11:51	66
11/3/2017 22:31	65	12/3/2017 15:36	54	13/3/2017 20:41	65	15/3/2017 21:46	65	17/3/2017 22:51	65	19/3/2017 11:56	66
11/3/2017 22:36	65	12/3/2017 15:41	66	13/3/2017 20:46	65	15/3/2017 21:51	65	17/3/2017 22:56	64	19/3/2017 12:01	58
11/3/2017 22:41	65	12/3/2017 15:46	54	13/3/2017 20:51	66	15/3/2017 21:56	66	18/3/2017 19:01	64	19/3/2017 12:06	62
11/3/2017 22:46	65	12/3/2017 15:51	66	13/3/2017 20:56	65	15/3/2017 22:01	65	18/3/2017 19:06	64	19/3/2017 12:11	63
11/3/2017 22:51	65	12/3/2017 15:56	66	13/3/2017 21:01	65	15/3/2017 22:06	65	18/3/2017 19:11	64	19/3/2017 12:16	63
11/3/2017 22:56	64	12/3/2017 16:01	66	13/3/2017 21:06	64	15/3/2017 22:11	65	18/3/2017 19:16	66	19/3/2017 12:21	63
12/3/2017 7:01	64	12/3/2017 16:06	66	13/3/2017 21:11	65	15/3/2017 22:16	65	18/3/2017 19:21	66	19/3/2017 12:26	64
12/3/2017 7:06	64	12/3/2017 16:11	66	13/3/2017 21:16	65	15/3/2017 22:21	65	18/3/2017 19:26	66	19/3/2017 12:31	63
12/3/2017 7:11	66	12/3/2017 16:16	65	13/3/2017 21:21	65	15/3/2017 22:26	66	18/3/2017 19:31	66	19/3/2017 12:36	65
12/3/2017 7:16	64	12/3/2017 16:21	66	13/3/2017 21:26	65	15/3/2017 22:31	66	18/3/2017 19:36	65	19/3/2017 12:41	64
12/3/2017 7:21	65	12/3/2017 16:26	58	13/3/2017 21:31	64	15/3/2017 22:36	65	18/3/2017 19:41	66	19/3/2017 12:46	63
12/3/2017 7:26	65	12/3/2017 16:31	66	13/3/2017 21:36	64	15/3/2017 22:41	66	18/3/2017 19:46	65	19/3/2017 12:51	64
12/3/2017 7:31	65	12/3/2017 16:36	62	13/3/2017 21:41	65	15/3/2017 22:46	65	18/3/2017 19:51	65	19/3/2017 12:56	49
12/3/2017 7:36	65	12/3/2017 16:41	66	13/3/2017 21:46	65	15/3/2017 22:51	66	18/3/2017 19:56	64	19/3/2017 13:01	65
12/3/2017 7:41	65	12/3/2017 16:46	65	13/3/2017 21:51	65	15/3/2017 22:56	64	18/3/2017 20:01	66	19/3/2017 13:06	59
12/3/2017 7:46	66	12/3/2017 16:51	66	13/3/2017 21:56	65	16/3/2017 19:01	66	18/3/2017 20:06	65	19/3/2017 13:11	63
12/3/2017 7:51	65	12/3/2017 16:56	53	13/3/2017 22:01	65	16/3/2017 19:06	55	18/3/2017 20:11	65	19/3/2017 13:16	59
12/3/2017 7:56	65	12/3/2017 17:01	66	13/3/2017 22:06	65	16/3/2017 19:11	49	18/3/2017 20:16	66	19/3/2017 13:21	62
12/3/2017 8:01	65	12/3/2017 17:06	65	13/3/2017 22:11	65	16/3/2017 19:16	66	18/3/2017 20:21	65	19/3/2017 13:26	61
12/3/2017 8:06	66	12/3/2017 17:11	65	13/3/2017 22:16	65	16/3/2017 19:21	66	18/3/2017 20:26	58	19/3/2017 13:31	59
12/3/2017 8:11	66	12/3/2017 17:16	66	13/3/2017 22:21	65	16/3/2017 19:26	66	18/3/2017 20:31	65	19/3/2017 13:36	61
12/3/2017 8:16	66	12/3/2017 17:21	66	13/3/2017 22:26	65	16/3/2017 19:31	66	18/3/2017 20:36	66	19/3/2017 13:41	59
12/3/2017 8:21	65	12/3/2017 17:26	66	13/3/2017 22:31	64	16/3/2017 19:36	59	18/3/2017 20:41	66	19/3/2017 13:46	57
12/3/2017 8:26	66	12/3/2017 17:31	66	13/3/2017 22:36	65	16/3/2017 19:41	66	18/3/2017 20:46	66	19/3/2017 13:51	46
12/3/2017 8:31	66	12/3/2017 17:36	66	13/3/2017 22:41	65	16/3/2017 19:46	66	18/3/2017 20:51	66	19/3/2017 13:56	59
12/3/2017 8:36	66	12/3/2017 17:41	66	13/3/2017 22:46	64	16/3/2017 19:51	58	18/3/2017 20:56	65	19/3/2017 14:01	57
12/3/2017 8:41	66	12/3/2017 17:46	65	13/3/2017 22:51	65	16/3/2017 19:56	59	18/3/2017 21:01	65	19/3/2017 14:06	55
12/3/2017 8:46	66	12/3/2017 17:51	66	13/3/2017 22:56	64	16/3/2017 20:01	66	18/3/2017 21:06	65	19/3/2017 14:11	66
12/3/2017 8:51	66	12/3/2017 17:56	66	14/3/2017 19:01	66	16/3/2017 20:06	66	18/3/2017 21:11	65	19/3/2017 14:16	66
12/3/2017 8:56	66	12/3/2017 18:01	66	14/3/2017 19:06	58	16/3/2017 20:11	66	18/3/2017 21:16	65	19/3/2017 14:21	58
12/3/2017 9:01	66	12/3/2017 18:06	66	14/3/2017 19:11	66	16/3/2017 20:16	55	18/3/2017 21:21	65	19/3/2017 14:26	66
12/3/2017 9:06	49	12/3/2017 18:11	66	14/3/2017 19:16	66	16/3/2017 20:21	66	18/3/2017 21:26	65	19/3/2017 14:31	51
12/3/2017 9:11	66	12/3/2017 18:16	66	14/3/2017 19:21	66	16/3/2017 20:26	66	18/3/2017 21:31	66	19/3/2017 14:36	57
12/3/2017 9:16	66	12/3/2017 18:21	66	14/3/2017 19:26	66	16/3/2017 20:31	66	18/3/2017 21:36	64	19/3/2017 14:41	57
12/3/2017 9:21	66	12/3/2017 18:26	53	14/3/2017 19:31	66	16/3/2017 20:36	66	18/3/2017 21:41	65	19/3/2017 14:46	57
12/3/2017 9:26	66	12/3/2017 18:31	66	14/3/2017 19:36	66	16/3/2017 20:41	60	18/3/2017 21:46	65	19/3/2017 14:51	61
12/3/2017 9:31	66	12/3/2017 18:36	65	14/3/2017 19:41	65	16/3/2017 20:46	65	18/3/2017 21:51	65	19/3/2017 14:56	61
12/3/2017 9:36	66	12/3/2017 18:41	66	14/3/2017 19:46							

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)						Night time: 23:00-07:00	
19/3/2017 18:01	66	21/3/2017 19:06	66	23/3/2017 20:11	55	25/3/2017 21:16	51	26/3/2017 14:21	66
19/3/2017 18:06	66	21/3/2017 19:11	65	23/3/2017 20:16	65	25/3/2017 21:21	65	26/3/2017 14:26	66
19/3/2017 18:11	66	21/3/2017 19:16	66	23/3/2017 20:21	66	25/3/2017 21:26	65	26/3/2017 14:31	65
19/3/2017 18:16	66	21/3/2017 19:21	66	23/3/2017 20:26	66	25/3/2017 21:31	65	26/3/2017 14:36	65
19/3/2017 18:21	66	21/3/2017 19:26	66	23/3/2017 20:31	66	25/3/2017 21:36	65	26/3/2017 14:41	66
19/3/2017 18:26	66	21/3/2017 19:31	66	23/3/2017 20:36	66	25/3/2017 21:41	65	26/3/2017 14:46	66
19/3/2017 18:31	66	21/3/2017 19:36	66	23/3/2017 20:41	65	25/3/2017 21:46	64	26/3/2017 14:51	66
19/3/2017 18:36	66	21/3/2017 19:41	66	23/3/2017 20:46	65	25/3/2017 21:51	64	26/3/2017 14:56	57
19/3/2017 18:41	66	21/3/2017 19:46	66	23/3/2017 20:51	65	25/3/2017 21:56	65	26/3/2017 15:01	66
19/3/2017 18:46	66	21/3/2017 19:51	66	23/3/2017 20:56	65	25/3/2017 22:01	65	26/3/2017 15:06	65
19/3/2017 18:51	66	21/3/2017 19:56	65	23/3/2017 21:01	65	25/3/2017 22:06	64	26/3/2017 15:11	66
19/3/2017 18:56	66	21/3/2017 20:01	66	23/3/2017 21:06	64	25/3/2017 22:11	65	26/3/2017 15:16	66
19/3/2017 19:01	66	21/3/2017 20:06	66	23/3/2017 21:11	65	25/3/2017 22:16	65	26/3/2017 15:21	66
19/3/2017 19:06	43	21/3/2017 20:11	65	23/3/2017 21:16	65	25/3/2017 22:21	65	26/3/2017 15:26	65
19/3/2017 19:11	66	21/3/2017 20:16	66	23/3/2017 21:21	66	25/3/2017 22:26	64	26/3/2017 15:31	66
19/3/2017 19:16	66	21/3/2017 20:21	55	23/3/2017 21:26	65	25/3/2017 22:31	65	26/3/2017 15:36	66
19/3/2017 19:21	66	21/3/2017 20:26	66	23/3/2017 21:31	65	25/3/2017 22:36	65	26/3/2017 15:41	65
19/3/2017 19:26	66	21/3/2017 20:31	66	23/3/2017 21:36	65	25/3/2017 22:41	66	26/3/2017 15:46	65
19/3/2017 19:31	66	21/3/2017 20:36	66	23/3/2017 21:41	65	25/3/2017 22:46	65	26/3/2017 15:51	65
19/3/2017 19:36	66	21/3/2017 20:41	66	23/3/2017 21:46	65	25/3/2017 22:51	66	26/3/2017 15:56	66
19/3/2017 19:41	66	21/3/2017 20:46	66	23/3/2017 21:51	65	25/3/2017 22:56	66	26/3/2017 16:01	65
19/3/2017 19:46	66	21/3/2017 20:51	66	23/3/2017 21:56	65	26/3/2017 7:01	64	26/3/2017 16:06	56
19/3/2017 19:51	49	21/3/2017 20:56	66	23/3/2017 22:01	65	26/3/2017 7:06	65	26/3/2017 16:11	66
19/3/2017 19:56	66	21/3/2017 21:01	65	23/3/2017 22:06	65	26/3/2017 7:11	64	26/3/2017 16:16	66
19/3/2017 20:01	66	21/3/2017 21:06	65	23/3/2017 22:11	65	26/3/2017 7:16	63	26/3/2017 16:21	66
19/3/2017 20:06	66	21/3/2017 21:11	65	23/3/2017 22:16	66	26/3/2017 7:21	63	26/3/2017 16:26	66
19/3/2017 20:11	66	21/3/2017 21:16	65	23/3/2017 22:21	65	26/3/2017 7:26	63	26/3/2017 16:31	66
19/3/2017 20:16	46	21/3/2017 21:21	65	23/3/2017 22:26	65	26/3/2017 7:31	64	26/3/2017 16:36	66
19/3/2017 20:21	66	21/3/2017 21:26	64	23/3/2017 22:31	66	26/3/2017 7:36	64	26/3/2017 16:41	66
19/3/2017 20:26	59	21/3/2017 21:31	64	23/3/2017 22:36	64	26/3/2017 7:41	64	26/3/2017 16:46	65
19/3/2017 20:31	66	21/3/2017 21:36	64	23/3/2017 22:41	66	26/3/2017 7:46	65	26/3/2017 16:51	66
19/3/2017 20:36	66	21/3/2017 21:41	64	23/3/2017 22:46	66	26/3/2017 7:51	64	26/3/2017 16:56	66
19/3/2017 20:41	66	21/3/2017 21:46	65	23/3/2017 22:51	65	26/3/2017 7:56	65	26/3/2017 17:01	66
19/3/2017 20:46	66	21/3/2017 21:51	64	23/3/2017 22:56	65	26/3/2017 8:01	64	26/3/2017 17:06	66
19/3/2017 20:51	66	21/3/2017 21:56	64	24/3/2017 19:01	64	26/3/2017 8:06	65	26/3/2017 17:11	66
19/3/2017 20:56	66	21/3/2017 22:01	64	24/3/2017 19:06	64	26/3/2017 8:11	64	26/3/2017 17:16	66
19/3/2017 21:01	66	21/3/2017 22:06	64	24/3/2017 19:11	66	26/3/2017 8:16	65	26/3/2017 17:21	66
19/3/2017 21:06	66	21/3/2017 22:11	65	24/3/2017 19:16	65	26/3/2017 8:21	65	26/3/2017 17:26	66
19/3/2017 21:11	65	21/3/2017 22:16	64	24/3/2017 19:21	66	26/3/2017 8:26	66	26/3/2017 17:31	66
19/3/2017 21:16	65	21/3/2017 22:21	65	24/3/2017 19:26	66	26/3/2017 8:31	65	26/3/2017 17:36	66
19/3/2017 21:21	65	21/3/2017 22:26	64	24/3/2017 19:31	66	26/3/2017 8:36	65	26/3/2017 17:41	66
19/3/2017 21:26	65	21/3/2017 22:31	64	24/3/2017 19:36	65	26/3/2017 8:41	65	26/3/2017 17:46	65
19/3/2017 21:31	66	21/3/2017 22:36	65	24/3/2017 19:41	65	26/3/2017 8:46	65	26/3/2017 17:51	66
19/3/2017 21:36	65	21/3/2017 22:41	64	24/3/2017 19:46	65	26/3/2017 8:51	66	26/3/2017 17:56	65
19/3/2017 21:41	65	21/3/2017 22:46	65	24/3/2017 19:51	66	26/3/2017 8:56	66	26/3/2017 18:01	53
19/3/2017 21:46	65	21/3/2017 22:51	65	24/3/2017 19:56	65	26/3/2017 9:01	65	26/3/2017 18:06	66
19/3/2017 21:51	66	21/3/2017 22:56	64	24/3/2017 20:01	49	26/3/2017 9:06	66	26/3/2017 18:11	65
19/3/2017 21:56	65	22/3/2017 19:01	66	24/3/2017 20:06	65	26/3/2017 9:11	66	26/3/2017 18:16	66
19/3/2017 22:01	65	22/3/2017 19:06	66	24/3/2017 20:11	66	26/3/2017 9:16	51	26/3/2017 18:21	52
19/3/2017 22:06	66	22/3/2017 19:11	65	24/3/2017 20:16	65	26/3/2017 9:21	66	26/3/2017 18:26	66
19/3/2017 22:11	65	22/3/2017 19:16	66	24/3/2017 20:21	65	26/3/2017 9:26	66	26/3/2017 18:31	66
19/3/2017 22:16	66	22/3/2017 19:21	65	24/3/2017 20:26	65	26/3/2017 9:31	53	26/3/2017 18:36	65
19/3/2017 22:21	65	22/3/2017 19:26	66	24/3/2017 20:31	65	26/3/2017 9:36	66	26/3/2017 18:41	66
19/3/2017 22:26	66	22/3/2017 19:31	65	24/3/2017 20:36	65	26/3/2017 9:41	66	26/3/2017 18:46	66
19/3/2017 22:31	65	22/3/2017 19:36	65	24/3/2017 20:41	65	26/3/2017 9:46	66	26/3/2017 18:51	66
19/3/2017 22:36	65	22/3/2017 19:41	66	24/3/2017 20:46	66	26/3/2017 9:51	66	26/3/2017 18:56	66
19/3/2017 22:41	65	22/3/2017 19:46	65	24/3/2017 20:51	65	26/3/2017 9:56	57	26/3/2017 19:01	65
19/3/2017 22:46	64	22/3/2017 19:51	66	24/3/2017 20:56	65	26/3/2017 10:01	66	26/3/2017 19:06	66
19/3/2017 22:51	64	22/3/2017 19:56	65	24/3/2017 21:01	65	26/3/2017 10:06	66	26/3/2017 19:11	65
19/3/2017 22:56	65	22/3/2017 20:01	66	24/3/2017 21:06	64	26/3/2017 10:11	66	26/3/2017 19:16	65
20/3/2017 19:01	62	22/3/2017 20:06	65	24/3/2017 21:11	66	26/3/2017 10:16	66	26/3/2017 19:21	66
20/3/2017 19:06	63	22/3/2017 20:11	65	24/3/2017 21:16	64	26/3/2017 10:21	66	26/3/2017 19:26	66
20/3/2017 19:11	61	22/3/2017 20:16	52	24/3/2017 21:21	65	26/3/2017 10:26	51	26/3/2017 19:31	66
20/3/2017 19:16	62	22/3/2017 20:21	66	24/3/2017 21:26	64	26/3/2017 10:31	66	26/3/2017 19:36	66
20/3/2017 19:21	63	22/3/2017 20:26	66	24/3/2017 21:31	65	26/3/2017 10:36	66	26/3/2017 19:41	65
20/3/2017 19:26	63	22/3/2017 20:31	65	24/3/2017 21:36	65	26/3/2017 10:41	66	26/3/2017 19:46	64
20/3/2017 19:31	63	22/3/2017 20:36	65	24/3/2017 21:41	65	26/3/2017 10:46	66	26/3/2017 19:51	65
20/3/2017 19:36	64	22/3/2017 20:41	65	24/3/2017 21:46	65	26/3/2017 10:51	66	26/3/2017 19:56	65
20/3/2017 19:41	51	22/3/2017 20:46	65	24/3/2017 21:51	65	26/3/2017 10:56	67	26/3/2017 20:01	65
20/3/2017 19:46	66	22/3/2017 20:51	65	24/3/2017 21:56	65	26/3/2017 11:01	66	26/3/2017 20:06	65
20/3/2017 19:51	66	22/3/2017 20:56	65	24/3/2017 22:01	65	26/3/2017 11:06	47	26/3/2017 20:11	66
20/3/2017 19:56	51	22/3/2017 21:01	65	24/3/2017 22:06	64	26/3/2017 11:11	66	26/3/2017 20:16	65
20/3/2017 20:01	66	22/3/2017 21:06	65	24/3/2017 22:11	66	26/3/2017 11:16	66	26/3/2017 20:21	65
20/3/2017 20:06	53	22/3/2017 21:11	65	24/3/2017 22:16	65	26/3/2017 11:21	66	26/3/2017 20:26	65
20/3/2017 20:11	66	22/3/2017 21:16	65	24/3/2017 22:21	65	26/3/2017 11:26	66	26/3/2017 20:31	65
20/3/2017 20:16	66	22/3/2017 21:21	65	24/3/2017 22:26	65	26/3/2017 11:31	66	26/3/2017 20:36	65
20/3/2017 20:21	66	22/3/2017 21:26	65	24/3/2017 22:31	65	26/3/2017 11:36	66	26/3/2017 20:41	64
20/3/2017 20:26	55	22/3/2017 21:31	65	24/3/2017 22:36	65	26/3/2017 11:41	66	26/3/2017 20:46	65
20/3/2017 20:31	66	22/3/2017 21:36	65	24/3/2017 22:41	66	26/3/2017 11:46	66	26/3/2017 20:51	66
20/3/2017 20:36	66	22/3/2017 21:41	64	24/3/2017 22:46	65	26/3/2017 11:51	57	26/3/2017 20:56	65
20/3/2017 20:41	60	22/3/2017 21:46	65	24/3/2017 22:51	65	26/3/2017 11:56	66	26/3/2017 21:01	65
20/3/2017 20:46	66	22/3/2017 21:51	65	24/3/2017 22:56	65	26/3/2017 12:01	66	26/3/2017 21:06	64
20/3/2017 20:51	66	22/3/2017 21:56	65	25/3/2017 19:01	66	26/3/2017 12:06	66	26/3/2017 21:11	65
20/3/2017 20:56	65	22/3/2017 22:01	65	25/3/2017 19:06	66	26/3/2017 12:11	66	26/3/2017 21:16	65
20/3/2017 21:01	65	22/3/2017 22:06	65	25/3/2017 19:11	65	26/3/2017 12:16	66	26/3/2017 21:21	65
20/3/2017 21:06	65	22/3/2017 22:11	64	25/3/2017 19:16	65	26/3/2017 12:21	66	26/3/2017 21:26	65
20/3/2017 21:11	65	22/3/2017 22:16	65	25/3/2017 19:21	65	26/3/2017 12:26	46	26/3/2017 21:31	65
20/3/2017 21:16	65	22/3/2017 22:21	65	25/3/201					

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
28/2/2017 0:56	65	1/3/2017 2:01	61	2/3/2017 3:06	59	3/3/2017 4:11	61	4/3/2017 5:16	63	5/3/2017 6:21	61
28/2/2017 1:01	62	1/3/2017 2:06	62	2/3/2017 3:11	59	3/3/2017 4:16	60	4/3/2017 5:21	61	5/3/2017 6:26	59
28/2/2017 1:06	60	1/3/2017 2:11	61	2/3/2017 3:16	60	3/3/2017 4:21	61	4/3/2017 5:26	60	5/3/2017 6:31	54
28/2/2017 1:11	63	1/3/2017 2:16	60	2/3/2017 3:21	60	3/3/2017 4:26	61	4/3/2017 5:31	63	5/3/2017 6:36	61
28/2/2017 1:16	61	1/3/2017 2:21	61	2/3/2017 3:26	60	3/3/2017 4:31	60	4/3/2017 5:36	61	5/3/2017 6:41	58
28/2/2017 1:21	63	1/3/2017 2:26	61	2/3/2017 3:31	60	3/3/2017 4:36	59	4/3/2017 5:41	62	5/3/2017 6:46	57
28/2/2017 1:26	62	1/3/2017 2:31	60	2/3/2017 3:36	60	3/3/2017 4:41	59	4/3/2017 5:46	62	5/3/2017 6:51	60
28/2/2017 1:31	63	1/3/2017 2:36	61	2/3/2017 3:41	59	3/3/2017 4:46	59	4/3/2017 5:51	62	5/3/2017 6:56	61
28/2/2017 1:36	62	1/3/2017 2:41	60	2/3/2017 3:46	59	3/3/2017 4:51	59	4/3/2017 5:56	63	5/3/2017 23:01	57
28/2/2017 1:41	62	1/3/2017 2:46	59	2/3/2017 3:51	60	3/3/2017 4:56	60	4/3/2017 6:01	63	5/3/2017 23:06	58
28/2/2017 1:46	62	1/3/2017 2:51	60	2/3/2017 3:56	59	3/3/2017 5:01	61	4/3/2017 6:06	63	5/3/2017 23:11	55
28/2/2017 1:51	62	1/3/2017 2:56	60	2/3/2017 4:01	58	3/3/2017 5:06	61	4/3/2017 6:11	62	5/3/2017 23:16	61
28/2/2017 1:56	61	1/3/2017 3:01	60	2/3/2017 4:06	59	3/3/2017 5:11	60	4/3/2017 6:16	40	5/3/2017 23:21	55
28/2/2017 2:01	62	1/3/2017 3:06	59	2/3/2017 4:11	58	3/3/2017 5:16	59	4/3/2017 6:21	54	5/3/2017 23:26	53
28/2/2017 2:06	61	1/3/2017 3:11	60	2/3/2017 4:16	61	3/3/2017 5:21	60	4/3/2017 6:26	55	5/3/2017 23:31	53
28/2/2017 2:11	61	1/3/2017 3:16	59	2/3/2017 4:21	59	3/3/2017 5:26	61	4/3/2017 6:31	63	5/3/2017 23:36	63
28/2/2017 2:16	61	1/3/2017 3:21	59	2/3/2017 4:26	58	3/3/2017 5:31	60	4/3/2017 6:36	59	5/3/2017 23:41	63
28/2/2017 2:21	62	1/3/2017 3:26	58	2/3/2017 4:31	60	3/3/2017 5:36	61	4/3/2017 6:41	58	5/3/2017 23:46	63
28/2/2017 2:26	61	1/3/2017 3:31	60	2/3/2017 4:36	59	3/3/2017 5:41	61	4/3/2017 6:46	60	5/3/2017 23:51	63
28/2/2017 2:31	60	1/3/2017 3:36	60	2/3/2017 4:41	59	3/3/2017 5:46	61	4/3/2017 6:51	60	5/3/2017 23:56	62
28/2/2017 2:36	61	1/3/2017 3:41	58	2/3/2017 4:46	61	3/3/2017 5:51	62	4/3/2017 6:56	62	6/3/2017 0:01	63
28/2/2017 2:41	60	1/3/2017 3:46	60	2/3/2017 4:51	60	3/3/2017 5:56	62	4/3/2017 23:01	61	6/3/2017 0:06	63
28/2/2017 2:46	61	1/3/2017 3:51	59	2/3/2017 4:56	59	3/3/2017 6:01	62	4/3/2017 23:06	60	6/3/2017 0:11	62
28/2/2017 2:51	61	1/3/2017 3:56	59	2/3/2017 5:01	60	3/3/2017 6:06	63	4/3/2017 23:11	60	6/3/2017 0:16	62
28/2/2017 2:56	59	1/3/2017 4:01	59	2/3/2017 5:06	60	3/3/2017 6:11	63	4/3/2017 23:16	61	6/3/2017 0:21	62
28/2/2017 3:01	60	1/3/2017 4:06	58	2/3/2017 5:11	60	3/3/2017 6:16	51	4/3/2017 23:21	60	6/3/2017 0:26	61
28/2/2017 3:06	61	1/3/2017 4:11	60	2/3/2017 5:16	61	3/3/2017 6:21	53	4/3/2017 23:26	60	6/3/2017 0:31	62
28/2/2017 3:11	60	1/3/2017 4:16	61	2/3/2017 5:21	60	3/3/2017 6:26	60	4/3/2017 23:31	58	6/3/2017 0:36	62
28/2/2017 3:16	60	1/3/2017 4:21	59	2/3/2017 5:26	63	3/3/2017 6:31	61	4/3/2017 23:36	59	6/3/2017 0:41	61
28/2/2017 3:21	62	1/3/2017 4:26	60	2/3/2017 5:31	61	3/3/2017 6:36	61	4/3/2017 23:41	61	6/3/2017 0:46	61
28/2/2017 3:26	61	1/3/2017 4:31	60	2/3/2017 5:36	61	3/3/2017 6:41	62	4/3/2017 23:46	59	6/3/2017 0:51	63
28/2/2017 3:31	60	1/3/2017 4:36	60	2/3/2017 5:41	62	3/3/2017 6:46	62	4/3/2017 23:51	53	6/3/2017 0:56	61
28/2/2017 3:36	60	1/3/2017 4:41	60	2/3/2017 5:46	61	3/3/2017 6:51	64	4/3/2017 23:56	52	6/3/2017 1:01	61
28/2/2017 3:41	59	1/3/2017 4:46	59	2/3/2017 5:51	62	3/3/2017 6:56	65	5/3/2017 0:01	56	6/3/2017 1:06	61
28/2/2017 3:46	60	1/3/2017 4:51	60	2/3/2017 5:56	63	3/3/2017 23:01	62	5/3/2017 0:06	59	6/3/2017 1:11	60
28/2/2017 3:51	60	1/3/2017 4:56	60	2/3/2017 6:01	62	3/3/2017 23:06	62	5/3/2017 0:11	56	6/3/2017 1:16	61
28/2/2017 3:56	59	1/3/2017 5:01	60	2/3/2017 6:06	48	3/3/2017 23:11	61	5/3/2017 0:16	50	6/3/2017 1:21	61
28/2/2017 4:01	58	1/3/2017 5:06	61	2/3/2017 6:11	63	3/3/2017 23:16	60	5/3/2017 0:21	56	6/3/2017 1:26	61
28/2/2017 4:06	59	1/3/2017 5:11	59	2/3/2017 6:16	57	3/3/2017 23:21	59	5/3/2017 0:26	53	6/3/2017 1:31	60
28/2/2017 4:11	59	1/3/2017 5:16	59	2/3/2017 6:21	57	3/3/2017 23:26	61	5/3/2017 0:31	57	6/3/2017 1:36	61
28/2/2017 4:16	59	1/3/2017 5:21	59	2/3/2017 6:26	59	3/3/2017 23:31	61	5/3/2017 0:36	53	6/3/2017 1:41	60
28/2/2017 4:21	59	1/3/2017 5:26	61	2/3/2017 6:31	60	3/3/2017 23:36	58	5/3/2017 0:41	63	6/3/2017 1:46	60
28/2/2017 4:26	60	1/3/2017 5:31	61	2/3/2017 6:36	59	3/3/2017 23:41	59	5/3/2017 0:46	51	6/3/2017 1:51	59
28/2/2017 4:31	60	1/3/2017 5:36	61	2/3/2017 6:41	62	3/3/2017 23:46	59	5/3/2017 0:51	63	6/3/2017 1:56	60
28/2/2017 4:36	59	1/3/2017 5:41	61	2/3/2017 6:46	64	3/3/2017 23:51	55	5/3/2017 0:56	50	6/3/2017 2:01	60
28/2/2017 4:41	59	1/3/2017 5:46	63	2/3/2017 6:51	64	3/3/2017 23:56	58	5/3/2017 1:01	63	6/3/2017 2:06	60
28/2/2017 4:46	60	1/3/2017 5:51	62	2/3/2017 6:56	63	4/3/2017 0:01	58	5/3/2017 1:06	63	6/3/2017 2:11	61
28/2/2017 4:51	60	1/3/2017 5:56	63	2/3/2017 23:01	60	4/3/2017 0:06	55	5/3/2017 1:11	62	6/3/2017 2:16	60
28/2/2017 4:56	60	1/3/2017 6:01	62	2/3/2017 23:06	60	4/3/2017 0:11	59	5/3/2017 1:16	63	6/3/2017 2:21	58
28/2/2017 5:01	60	1/3/2017 6:06	63	2/3/2017 23:11	65	4/3/2017 0:16	57	5/3/2017 1:21	62	6/3/2017 2:26	58
28/2/2017 5:06	59	1/3/2017 6:11	63	2/3/2017 23:16	63	4/3/2017 0:21	56	5/3/2017 1:26	50	6/3/2017 2:31	58
28/2/2017 5:11	59	1/3/2017 6:16	63	2/3/2017 23:21	57	4/3/2017 0:26	59	5/3/2017 1:31	63	6/3/2017 2:36	58
28/2/2017 5:16	60	1/3/2017 6:21	37	2/3/2017 23:26	60	4/3/2017 0:31	60	5/3/2017 1:36	63	6/3/2017 2:41	58
28/2/2017 5:21	61	1/3/2017 6:26	60	2/3/2017 23:31	58	4/3/2017 0:36	57	5/3/2017 1:41	62	6/3/2017 2:46	59
28/2/2017 5:26	62	1/3/2017 6:31	59	2/3/2017 23:36	57	4/3/2017 0:41	51	5/3/2017 1:46	63	6/3/2017 2:51	57
28/2/2017 5:31	61	1/3/2017 6:36	58	2/3/2017 23:41	57	4/3/2017 0:46	50	5/3/2017 1:51	62	6/3/2017 2:56	59
28/2/2017 5:36	61	1/3/2017 6:41	61	2/3/2017 23:46	58	4/3/2017 0:51	55	5/3/2017 1:56	62	6/3/2017 3:01	59
28/2/2017 5:41	61	1/3/2017 6:46	62	2/3/2017 23:51	53	4/3/2017 0:56	55	5/3/2017 2:01	62	6/3/2017 3:06	61
28/2/2017 5:46	62	1/3/2017 6:51	64	2/3/2017 23:56	52	4/3/2017 1:01	55	5/3/2017 2:06	62	6/3/2017 3:11	58
28/2/2017 5:51	62	1/3/2017 6:56	63	3/3/2017 0:01	56	4/3/2017 1:06	63	5/3/2017 2:11	61	6/3/2017 3:16	59
28/2/2017 5:56	62	1/3/2017 23:01	61	3/3/2017 0:06	51	4/3/2017 1:11	59	5/3/2017 2:16	62	6/3/2017 3:21	58
28/2/2017 6:01	63	1/3/2017 23:06	59	3/3/2017 0:11	55	4/3/2017 1:16	64	5/3/2017 2:21	56	6/3/2017 3:26	58
28/2/2017 6:06	59	1/3/2017 23:11	62	3/3/2017 0:16	52	4/3/2017 1:21	63	5/3/2017 2:26	61	6/3/2017 3:31	60
28/2/2017 6:11	54	1/3/2017 23:16	60	3/3/2017 0:21	59	4/3/2017 1:26	50	5/3/2017 2:31	62	6/3/2017 3:36	58
28/2/2017 6:16	55	1/3/2017 23:21	59	3/3/2017 0:26	54	4/3/2017 1:31	63	5/3/2017 2:36	61	6/3/2017 3:41	59
28/2/2017 6:21	60	1/3/2017 23:26	60	3/3/2017 0:31	63	4/3/2017 1:36	63	5/3/2017 2:41	62	6/3/2017 3:46	58
28/2/2017 6:26	60	1/3/2017 23:31	58	3/3/2017 0:36	45	4/3/2017 1:41	58	5/3/2017 2:46	62	6/3/2017 3:51	58
28/2/2017 6:31	62	1/3/2017 23:36	59	3/3/2017 0:41	63	4/3/2017 1:46	59	5/3/2017 2:51	61	6/3/2017 3:56	58
28/2/2017 6:36	61	1/3/2017 23:41	58	3/3/2017 0:46	63	4/3/2017 1:51	57	5/3/2017 2:56	61	6/3/2017 4:01	56
28/2/2017 6:41	62	1/3/2017 23:46	59	3/3/2017 0:51	62	4/3/2017 1:56	62	5/3/2017 3:01	60	6/3/2017 4:06	58
28/2/2017 6:46	65	1/3/2017 23:51	56	3/3/2017 0:56	63	4/3/2017 2:01	54	5/3/2017 3:06	61	6/3/2017 4:11	58
28/2/2017 6:51	63	1/3/2017 23:56	55	3/3/2017 1:01	51	4/3/2017 2:06	62	5/3/2017 3:11	61	6/3/2017 4:16	58
28/2/2017 6:56	63	2/3/2017 0:01	56	3/3/2017 1:06	62	4/3/2017 2:11	61	5/3/2017 3:16	61	6/3/2017 4:21	58
28/2/2017 23:01	60	2/3/2017 0:06	56	3/3/2017 1:11	63	4/3/2017 2:16	62	5/3/2017 3:21	61	6/3/2017 4:26	58
28/2/2017 23:06	58	2/3/2017 0:11	54	3/3/2017 1:16	63	4/3/2017 2:21	62	5/3/2017 3:26	61	6/3/2017 4:31	60
28/2/2017 23:11	59	2/3/2017 0:16	63	3/3/2017 1:21	62	4/3/2017 2:26	63	5/3/2017 3:31	62	6/3/2017 4:36	59
28/2/2017 23:16	59	2/3/2017 0:21	52	3/3/2017 1:26	62	4/3/2017 2:31	62	5/3/2017 3:36	61	6/3/2017 4:41	57
28/2/2017 23:21	58	2/3/2017 0:26	57	3/3/2017 1:31	62	4/3/2017 2:36	62	5/3/2017 3:41	61	6/3/2017 4:46</	

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
6/3/2017 23:26	57	8/3/2017 0:31	63	9/3/2017 1:36	62	10/3/2017 2:41	61	11/3/2017 3:46	60	12/3/2017 4:51	60
6/3/2017 23:31	42	8/3/2017 0:36	63	9/3/2017 1:41	62	10/3/2017 2:46	61	11/3/2017 3:51	59	12/3/2017 4:56	61
6/3/2017 23:36	52	8/3/2017 0:41	62	9/3/2017 1:46	62	10/3/2017 2:51	61	11/3/2017 3:56	61	12/3/2017 5:01	61
6/3/2017 23:41	49	8/3/2017 0:46	62	9/3/2017 1:51	61	10/3/2017 2:56	61	11/3/2017 4:01	59	12/3/2017 5:06	61
6/3/2017 23:46	55	8/3/2017 0:51	62	9/3/2017 1:56	61	10/3/2017 3:01	61	11/3/2017 4:06	59	12/3/2017 5:11	61
6/3/2017 23:51	56	8/3/2017 0:56	62	9/3/2017 2:01	62	10/3/2017 3:06	59	11/3/2017 4:11	59	12/3/2017 5:16	61
6/3/2017 23:56	63	8/3/2017 1:01	63	9/3/2017 2:06	61	10/3/2017 3:11	59	11/3/2017 4:16	60	12/3/2017 5:21	62
7/3/2017 0:01	56	8/3/2017 1:06	63	9/3/2017 2:11	61	10/3/2017 3:16	59	11/3/2017 4:21	61	12/3/2017 5:26	61
7/3/2017 0:06	63	8/3/2017 1:11	63	9/3/2017 2:16	61	10/3/2017 3:21	60	11/3/2017 4:26	61	12/3/2017 5:31	61
7/3/2017 0:11	46	8/3/2017 1:16	62	9/3/2017 2:21	58	10/3/2017 3:26	59	11/3/2017 4:31	60	12/3/2017 5:36	62
7/3/2017 0:16	55	8/3/2017 1:21	62	9/3/2017 2:26	62	10/3/2017 3:31	60	11/3/2017 4:36	60	12/3/2017 5:41	62
7/3/2017 0:21	49	8/3/2017 1:26	61	9/3/2017 2:31	61	10/3/2017 3:36	60	11/3/2017 4:41	60	12/3/2017 5:46	63
7/3/2017 0:26	63	8/3/2017 1:31	61	9/3/2017 2:36	61	10/3/2017 3:41	59	11/3/2017 4:46	60	12/3/2017 5:51	63
7/3/2017 0:31	63	8/3/2017 1:36	61	9/3/2017 2:41	60	10/3/2017 3:46	61	11/3/2017 4:51	60	12/3/2017 5:56	62
7/3/2017 0:36	63	8/3/2017 1:41	61	9/3/2017 2:46	60	10/3/2017 3:51	60	11/3/2017 4:56	60	12/3/2017 6:01	63
7/3/2017 0:41	63	8/3/2017 1:46	61	9/3/2017 2:51	60	10/3/2017 3:56	59	11/3/2017 5:01	61	12/3/2017 6:06	63
7/3/2017 0:46	62	8/3/2017 1:51	61	9/3/2017 2:56	59	10/3/2017 4:01	62	11/3/2017 5:06	61	12/3/2017 6:11	48
7/3/2017 0:51	49	8/3/2017 1:56	62	9/3/2017 3:01	60	10/3/2017 4:06	61	11/3/2017 5:11	61	12/3/2017 6:16	63
7/3/2017 0:56	63	8/3/2017 2:01	61	9/3/2017 3:06	60	10/3/2017 4:11	59	11/3/2017 5:16	61	12/3/2017 6:21	52
7/3/2017 1:01	63	8/3/2017 2:06	61	9/3/2017 3:11	60	10/3/2017 4:16	59	11/3/2017 5:21	61	12/3/2017 6:26	46
7/3/2017 1:06	62	8/3/2017 2:11	61	9/3/2017 3:16	60	10/3/2017 4:21	61	11/3/2017 5:26	62	12/3/2017 6:31	57
7/3/2017 1:11	62	8/3/2017 2:16	60	9/3/2017 3:21	59	10/3/2017 4:26	60	11/3/2017 5:31	62	12/3/2017 6:36	55
7/3/2017 1:16	62	8/3/2017 2:21	61	9/3/2017 3:26	59	10/3/2017 4:31	59	11/3/2017 5:36	63	12/3/2017 6:41	60
7/3/2017 1:21	62	8/3/2017 2:26	60	9/3/2017 3:31	59	10/3/2017 4:36	59	11/3/2017 5:41	61	12/3/2017 6:46	59
7/3/2017 1:26	62	8/3/2017 2:31	60	9/3/2017 3:36	60	10/3/2017 4:41	60	11/3/2017 5:46	62	12/3/2017 6:51	58
7/3/2017 1:31	61	8/3/2017 2:36	61	9/3/2017 3:41	61	10/3/2017 4:46	58	11/3/2017 5:51	62	12/3/2017 6:56	59
7/3/2017 1:36	62	8/3/2017 2:41	60	9/3/2017 3:46	60	10/3/2017 4:51	60	11/3/2017 5:56	62	12/3/2017 7:01	57
7/3/2017 1:41	61	8/3/2017 2:46	60	9/3/2017 3:51	59	10/3/2017 4:56	60	11/3/2017 6:01	61	12/3/2017 7:06	56
7/3/2017 1:46	62	8/3/2017 2:51	60	9/3/2017 3:56	60	10/3/2017 5:01	61	11/3/2017 6:06	62	12/3/2017 7:11	57
7/3/2017 1:51	61	8/3/2017 2:56	59	9/3/2017 4:01	59	10/3/2017 5:06	59	11/3/2017 6:11	63	12/3/2017 7:16	53
7/3/2017 1:56	61	8/3/2017 3:01	59	9/3/2017 4:06	60	10/3/2017 5:11	59	11/3/2017 6:16	62	12/3/2017 7:21	53
7/3/2017 2:01	61	8/3/2017 3:06	60	9/3/2017 4:11	59	10/3/2017 5:16	60	11/3/2017 6:21	63	12/3/2017 7:26	53
7/3/2017 2:06	60	8/3/2017 3:11	60	9/3/2017 4:16	60	10/3/2017 5:21	60	11/3/2017 6:26	50	12/3/2017 7:31	63
7/3/2017 2:11	62	8/3/2017 3:16	58	9/3/2017 4:21	61	10/3/2017 5:26	62	11/3/2017 6:31	51	12/3/2017 7:36	63
7/3/2017 2:16	60	8/3/2017 3:21	58	9/3/2017 4:26	61	10/3/2017 5:31	61	11/3/2017 6:36	55	12/3/2017 7:41	58
7/3/2017 2:21	59	8/3/2017 3:26	60	9/3/2017 4:31	61	10/3/2017 5:36	62	11/3/2017 6:41	58	12/3/2017 7:46	56
7/3/2017 2:26	62	8/3/2017 3:31	59	9/3/2017 4:36	59	10/3/2017 5:41	62	11/3/2017 6:46	59	12/3/2017 7:51	49
7/3/2017 2:31	60	8/3/2017 3:36	59	9/3/2017 4:41	61	10/3/2017 5:46	62	11/3/2017 6:51	61	12/3/2017 7:56	52
7/3/2017 2:36	61	8/3/2017 3:41	59	9/3/2017 4:46	60	10/3/2017 5:51	61	11/3/2017 6:56	55	13/3/2017 0:01	52
7/3/2017 2:41	60	8/3/2017 3:46	59	9/3/2017 4:51	59	10/3/2017 5:56	62	11/3/2017 7:01	63	13/3/2017 0:06	62
7/3/2017 2:46	60	8/3/2017 3:51	59	9/3/2017 4:56	60	10/3/2017 6:01	62	11/3/2017 7:06	62	13/3/2017 0:11	63
7/3/2017 2:51	59	8/3/2017 3:56	59	9/3/2017 5:01	60	10/3/2017 6:06	63	11/3/2017 7:11	59	13/3/2017 0:16	63
7/3/2017 2:56	59	8/3/2017 4:01	58	9/3/2017 5:06	60	10/3/2017 6:11	62	11/3/2017 7:16	59	13/3/2017 0:21	62
7/3/2017 3:01	60	8/3/2017 4:06	60	9/3/2017 5:11	60	10/3/2017 6:16	63	11/3/2017 7:21	59	13/3/2017 0:26	62
7/3/2017 3:06	59	8/3/2017 4:11	59	9/3/2017 5:16	60	10/3/2017 6:21	63	11/3/2017 7:26	58	13/3/2017 0:31	62
7/3/2017 3:11	59	8/3/2017 4:16	59	9/3/2017 5:21	60	10/3/2017 6:26	58	11/3/2017 7:31	57	13/3/2017 0:36	63
7/3/2017 3:16	59	8/3/2017 4:21	60	9/3/2017 5:26	61	10/3/2017 6:31	58	11/3/2017 7:36	58	13/3/2017 0:41	63
7/3/2017 3:21	59	8/3/2017 4:26	58	9/3/2017 5:31	61	10/3/2017 6:36	61	11/3/2017 7:41	59	13/3/2017 0:46	63
7/3/2017 3:26	59	8/3/2017 4:31	60	9/3/2017 5:36	61	10/3/2017 6:41	63	11/3/2017 7:46	58	13/3/2017 0:51	60
7/3/2017 3:31	60	8/3/2017 4:36	60	9/3/2017 5:41	61	10/3/2017 6:46	62	11/3/2017 7:51	56	13/3/2017 0:56	63
7/3/2017 3:36	59	8/3/2017 4:41	60	9/3/2017 5:46	61	10/3/2017 6:51	62	11/3/2017 7:56	58	13/3/2017 1:01	62
7/3/2017 3:41	61	8/3/2017 4:46	59	9/3/2017 5:51	61	10/3/2017 6:56	64	12/3/2017 0:01	59	13/3/2017 1:06	62
7/3/2017 3:46	59	8/3/2017 4:51	60	9/3/2017 5:56	60	10/3/2017 7:01	61	12/3/2017 0:06	55	13/3/2017 1:11	60
7/3/2017 3:51	60	8/3/2017 4:56	61	9/3/2017 6:01	62	10/3/2017 7:06	56	12/3/2017 0:11	58	13/3/2017 1:16	60
7/3/2017 3:56	59	8/3/2017 5:01	59	9/3/2017 6:06	63	10/3/2017 7:11	57	12/3/2017 0:16	55	13/3/2017 1:21	60
7/3/2017 4:01	59	8/3/2017 5:06	59	9/3/2017 6:11	63	10/3/2017 7:16	57	12/3/2017 0:21	40	13/3/2017 1:26	60
7/3/2017 4:06	59	8/3/2017 5:11	60	9/3/2017 6:16	54	10/3/2017 7:21	59	12/3/2017 0:26	55	13/3/2017 1:31	61
7/3/2017 4:11	59	8/3/2017 5:16	61	9/3/2017 6:21	55	10/3/2017 7:26	59	12/3/2017 0:31	54	13/3/2017 1:36	60
7/3/2017 4:16	59	8/3/2017 5:21	60	9/3/2017 6:26	59	10/3/2017 7:31	57	12/3/2017 0:36	45	13/3/2017 1:41	60
7/3/2017 4:21	60	8/3/2017 5:26	61	9/3/2017 6:31	59	10/3/2017 7:36	54	12/3/2017 0:41	62	13/3/2017 1:46	60
7/3/2017 4:26	60	8/3/2017 5:31	61	9/3/2017 6:36	61	10/3/2017 7:41	57	12/3/2017 0:46	50	13/3/2017 1:51	61
7/3/2017 4:31	60	8/3/2017 5:36	61	9/3/2017 6:41	62	10/3/2017 7:46	55	12/3/2017 0:51	63	13/3/2017 1:56	61
7/3/2017 4:36	59	8/3/2017 5:41	61	9/3/2017 6:46	61	10/3/2017 7:51	51	12/3/2017 0:56	63	13/3/2017 2:01	59
7/3/2017 4:41	61	8/3/2017 5:46	61	9/3/2017 6:51	64	10/3/2017 7:56	53	12/3/2017 1:01	53	13/3/2017 2:06	60
7/3/2017 4:46	60	8/3/2017 5:51	61	9/3/2017 6:56	63	11/3/2017 0:01	61	12/3/2017 1:06	60	13/3/2017 2:11	60
7/3/2017 4:51	61	8/3/2017 5:56	63	9/3/2017 7:01	58	11/3/2017 0:06	63	12/3/2017 1:11	58	13/3/2017 2:16	59
7/3/2017 4:56	60	8/3/2017 6:01	61	9/3/2017 7:06	58	11/3/2017 0:11	63	12/3/2017 1:16	56	13/3/2017 2:21	59
7/3/2017 5:01	60	8/3/2017 6:06	45	9/3/2017 7:11	58	11/3/2017 0:16	63	12/3/2017 1:21	52	13/3/2017 2:26	60
7/3/2017 5:06	59	8/3/2017 6:11	62	9/3/2017 7:16	58	11/3/2017 0:21	63	12/3/2017 1:26	54	13/3/2017 2:31	60
7/3/2017 5:11	60	8/3/2017 6:16	55	9/3/2017 7:21	60	11/3/2017 0:26	43	12/3/2017 1:31	63	13/3/2017 2:36	59
7/3/2017 5:16	61	8/3/2017 6:21	54	9/3/2017 7:26	60	11/3/2017 0:31	60	12/3/2017 1:36	63	13/3/2017 2:41	58
7/3/2017 5:21	60	8/3/2017 6:26	55	9/3/2017 7:31	59	11/3/2017 0:36	63	12/3/2017 1:41	50	13/3/2017 2:46	60
7/3/2017 5:26	61	8/3/2017 6:31	60	9/3/2017 7:36	58	11/3/2017 0:41	49	12/3/2017 1:46	53	13/3/2017 2:51	58
7/3/2017 5:31	61	8/3/2017 6:36	60	9/3/2017 7:41	57	11/3/2017 0:46	51	12/3/2017 1:51	62	13/3/2017 2:56	58
7/3/2017 5:36	62	8/3/2017 6:41	61	9/3/2017 7:46	55	11/3/2017 0:51	62	12/3/2017 1:56	63	13/3/2017 3:01	58
7/3/2017 5:41	62	8/3/2017 6:46	61	9/3/2017 7:51	49	11/3/2017 0:56	63	12/3/2017 2:01	57	13/3/2017 3:06	60
7/3/2017 5:46	62	8/3/2017 6:51	72	9/3/2017 7:56	57	11/3/2017 1:01	63	12/3/2017 2:06	62	13/3/2017 3:11	60
7/3/2017 5:51	62	8/3/2017 6:56	6								

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
13/3/2017 5:56	62	14/3/2017 23:01	61	16/3/2017 0:06	55	17/3/2017 1:11	52	18/3/2017 2:16	62	19/3/2017 3:21	61
13/3/2017 6:01	62	14/3/2017 23:06	59	16/3/2017 0:11	53	17/3/2017 1:16	62	18/3/2017 2:21	62	19/3/2017 3:26	62
13/3/2017 6:06	63	14/3/2017 23:11	58	16/3/2017 0:16	63	17/3/2017 1:21	62	18/3/2017 2:26	63	19/3/2017 3:31	61
13/3/2017 6:11	63	14/3/2017 23:16	60	16/3/2017 0:21	48	17/3/2017 1:26	62	18/3/2017 2:31	62	19/3/2017 3:36	61
13/3/2017 6:16	63	14/3/2017 23:21	60	16/3/2017 0:26	54	17/3/2017 1:31	65	18/3/2017 2:36	62	19/3/2017 3:41	60
13/3/2017 6:21	56	14/3/2017 23:26	59	16/3/2017 0:31	63	17/3/2017 1:36	63	18/3/2017 2:41	61	19/3/2017 3:46	61
13/3/2017 6:26	54	14/3/2017 23:31	60	16/3/2017 0:36	56	17/3/2017 1:41	62	18/3/2017 2:46	63	19/3/2017 3:51	60
13/3/2017 6:31	59	14/3/2017 23:36	60	16/3/2017 0:41	48	17/3/2017 1:46	60	18/3/2017 2:51	62	19/3/2017 3:56	60
13/3/2017 6:36	59	14/3/2017 23:41	57	16/3/2017 0:46	63	17/3/2017 1:51	62	18/3/2017 2:56	61	19/3/2017 4:01	60
13/3/2017 6:41	60	14/3/2017 23:46	57	16/3/2017 0:51	63	17/3/2017 1:56	62	18/3/2017 3:01	62	19/3/2017 4:06	60
13/3/2017 6:46	61	14/3/2017 23:51	56	16/3/2017 0:56	63	17/3/2017 2:01	60	18/3/2017 3:06	61	19/3/2017 4:11	60
13/3/2017 6:51	62	14/3/2017 23:56	52	16/3/2017 1:01	62	17/3/2017 2:06	61	18/3/2017 3:11	62	19/3/2017 4:16	60
13/3/2017 6:56	63	15/3/2017 0:01	57	16/3/2017 1:06	63	17/3/2017 2:11	60	18/3/2017 3:16	62	19/3/2017 4:21	61
13/3/2017 23:01	62	15/3/2017 0:06	53	16/3/2017 1:11	62	17/3/2017 2:16	61	18/3/2017 3:21	61	19/3/2017 4:26	61
13/3/2017 23:06	58	15/3/2017 0:11	48	16/3/2017 1:16	62	17/3/2017 2:21	62	18/3/2017 3:26	60	19/3/2017 4:31	60
13/3/2017 23:11	58	15/3/2017 0:16	57	16/3/2017 1:21	62	17/3/2017 2:26	61	18/3/2017 3:31	61	19/3/2017 4:36	60
13/3/2017 23:16	57	15/3/2017 0:21	54	16/3/2017 1:26	62	17/3/2017 2:31	60	18/3/2017 3:36	61	19/3/2017 4:41	60
13/3/2017 23:21	59	15/3/2017 0:26	60	16/3/2017 1:31	62	17/3/2017 2:36	61	18/3/2017 3:41	61	19/3/2017 4:46	60
13/3/2017 23:26	55	15/3/2017 0:31	50	16/3/2017 1:36	62	17/3/2017 2:41	60	18/3/2017 3:46	60	19/3/2017 4:51	59
13/3/2017 23:31	50	15/3/2017 0:36	51	16/3/2017 1:41	62	17/3/2017 2:46	60	18/3/2017 3:51	61	19/3/2017 4:56	60
13/3/2017 23:36	53	15/3/2017 0:41	63	16/3/2017 1:46	62	17/3/2017 2:51	61	18/3/2017 3:56	61	19/3/2017 5:01	60
13/3/2017 23:41	50	15/3/2017 0:46	63	16/3/2017 1:51	62	17/3/2017 2:56	61	18/3/2017 4:01	60	19/3/2017 5:06	61
13/3/2017 23:46	55	15/3/2017 0:51	62	16/3/2017 1:56	61	17/3/2017 3:01	60	18/3/2017 4:06	61	19/3/2017 5:11	60
13/3/2017 23:51	62	15/3/2017 0:56	62	16/3/2017 2:01	62	17/3/2017 3:06	61	18/3/2017 4:11	61	19/3/2017 5:16	60
13/3/2017 23:56	63	15/3/2017 1:01	63	16/3/2017 2:06	61	17/3/2017 3:11	59	18/3/2017 4:16	60	19/3/2017 5:21	60
14/3/2017 0:01	37	15/3/2017 1:06	62	16/3/2017 2:11	61	17/3/2017 3:16	59	18/3/2017 4:21	62	19/3/2017 5:26	61
14/3/2017 0:06	63	15/3/2017 1:11	62	16/3/2017 2:16	60	17/3/2017 3:21	60	18/3/2017 4:26	62	19/3/2017 5:31	60
14/3/2017 0:11	63	15/3/2017 1:16	63	16/3/2017 2:21	60	17/3/2017 3:26	60	18/3/2017 4:31	61	19/3/2017 5:36	62
14/3/2017 0:16	62	15/3/2017 1:21	62	16/3/2017 2:26	62	17/3/2017 3:31	60	18/3/2017 4:36	60	19/3/2017 5:41	62
14/3/2017 0:21	63	15/3/2017 1:26	61	16/3/2017 2:31	60	17/3/2017 3:36	58	18/3/2017 4:41	61	19/3/2017 5:46	61
14/3/2017 0:26	63	15/3/2017 1:31	62	16/3/2017 2:36	62	17/3/2017 3:41	59	18/3/2017 4:46	61	19/3/2017 5:51	62
14/3/2017 0:31	62	15/3/2017 1:36	62	16/3/2017 2:41	61	17/3/2017 3:46	60	18/3/2017 4:51	61	19/3/2017 5:56	62
14/3/2017 0:36	62	15/3/2017 1:41	61	16/3/2017 2:46	61	17/3/2017 3:51	60	18/3/2017 4:56	60	19/3/2017 6:01	61
14/3/2017 0:41	63	15/3/2017 1:46	61	16/3/2017 2:51	61	17/3/2017 3:56	62	18/3/2017 5:01	60	19/3/2017 6:06	62
14/3/2017 0:46	62	15/3/2017 1:51	61	16/3/2017 2:56	60	17/3/2017 4:01	59	18/3/2017 5:06	62	19/3/2017 6:11	61
14/3/2017 0:51	63	15/3/2017 1:56	62	16/3/2017 3:01	60	17/3/2017 4:06	60	18/3/2017 5:11	59	19/3/2017 6:16	62
14/3/2017 0:56	61	15/3/2017 2:01	61	16/3/2017 3:06	60	17/3/2017 4:11	59	18/3/2017 5:16	61	19/3/2017 6:21	63
14/3/2017 1:01	62	15/3/2017 2:06	61	16/3/2017 3:11	62	17/3/2017 4:16	59	18/3/2017 5:21	61	19/3/2017 6:26	63
14/3/2017 1:06	62	15/3/2017 2:11	61	16/3/2017 3:16	59	17/3/2017 4:21	60	18/3/2017 5:26	62	19/3/2017 6:31	53
14/3/2017 1:11	61	15/3/2017 2:16	62	16/3/2017 3:21	60	17/3/2017 4:26	59	18/3/2017 5:31	61	19/3/2017 6:36	57
14/3/2017 1:16	61	15/3/2017 2:21	62	16/3/2017 3:26	60	17/3/2017 4:31	58	18/3/2017 5:36	63	19/3/2017 6:41	54
14/3/2017 1:21	63	15/3/2017 2:26	61	16/3/2017 3:31	61	17/3/2017 4:36	59	18/3/2017 5:41	61	19/3/2017 6:46	58
14/3/2017 1:26	61	15/3/2017 2:31	60	16/3/2017 3:36	60	17/3/2017 4:41	60	18/3/2017 5:46	62	19/3/2017 6:51	54
14/3/2017 1:31	61	15/3/2017 2:36	61	16/3/2017 3:41	59	17/3/2017 4:46	59	18/3/2017 5:51	61	19/3/2017 6:56	63
14/3/2017 1:36	61	15/3/2017 2:41	60	16/3/2017 3:46	60	17/3/2017 4:51	59	18/3/2017 5:56	62	19/3/2017 7:01	60
14/3/2017 1:41	61	15/3/2017 2:46	60	16/3/2017 3:51	59	17/3/2017 4:56	60	18/3/2017 6:01	62	19/3/2017 7:06	59
14/3/2017 1:46	61	15/3/2017 2:51	60	16/3/2017 3:56	60	17/3/2017 5:01	61	18/3/2017 6:06	62	19/3/2017 7:11	58
14/3/2017 1:51	61	15/3/2017 2:56	61	16/3/2017 4:01	59	17/3/2017 5:06	60	18/3/2017 6:11	62	19/3/2017 7:16	57
14/3/2017 1:56	61	15/3/2017 3:01	59	16/3/2017 4:06	59	17/3/2017 5:11	60	18/3/2017 6:16	58	19/3/2017 7:21	53
14/3/2017 2:01	59	15/3/2017 3:06	59	16/3/2017 4:11	59	17/3/2017 5:16	61	18/3/2017 6:21	58	19/3/2017 7:26	58
14/3/2017 2:06	60	15/3/2017 3:11	60	16/3/2017 4:16	60	17/3/2017 5:21	61	18/3/2017 6:26	62	19/3/2017 7:31	58
14/3/2017 2:11	61	15/3/2017 3:16	59	16/3/2017 4:21	61	17/3/2017 5:26	60	18/3/2017 6:31	62	19/3/2017 7:36	63
14/3/2017 2:16	60	15/3/2017 3:21	60	16/3/2017 4:26	61	17/3/2017 5:31	61	18/3/2017 6:36	55	19/3/2017 7:41	56
14/3/2017 2:21	60	15/3/2017 3:26	60	16/3/2017 4:31	60	17/3/2017 5:36	60	18/3/2017 6:41	58	19/3/2017 7:46	58
14/3/2017 2:26	60	15/3/2017 3:31	60	16/3/2017 4:36	60	17/3/2017 5:41	53	18/3/2017 6:46	57	19/3/2017 7:51	56
14/3/2017 2:31	59	15/3/2017 3:36	60	16/3/2017 4:41	59	17/3/2017 5:46	62	18/3/2017 6:51	58	19/3/2017 7:56	53
14/3/2017 2:36	59	15/3/2017 3:41	59	16/3/2017 4:46	60	17/3/2017 5:51	62	18/3/2017 6:56	60	20/3/2017 0:01	63
14/3/2017 2:41	60	15/3/2017 3:46	61	16/3/2017 4:51	60	17/3/2017 5:56	62	18/3/2017 7:01	60	20/3/2017 0:06	62
14/3/2017 2:46	60	15/3/2017 3:51	61	16/3/2017 4:56	60	17/3/2017 6:01	63	18/3/2017 7:06	60	20/3/2017 0:11	48
14/3/2017 2:51	60	15/3/2017 3:56	59	16/3/2017 5:01	60	17/3/2017 6:06	63	18/3/2017 7:11	60	20/3/2017 0:16	45
14/3/2017 2:56	61	15/3/2017 4:01	59	16/3/2017 5:06	61	17/3/2017 6:11	54	18/3/2017 7:16	61	20/3/2017 0:21	62
14/3/2017 3:01	59	15/3/2017 4:06	61	16/3/2017 5:11	60	17/3/2017 6:16	60	18/3/2017 7:21	60	20/3/2017 0:26	63
14/3/2017 3:06	60	15/3/2017 4:11	61	16/3/2017 5:16	61	17/3/2017 6:21	51	18/3/2017 7:26	59	20/3/2017 0:31	54
14/3/2017 3:11	60	15/3/2017 4:16	60	16/3/2017 5:21	60	17/3/2017 6:26	55	18/3/2017 7:31	60	20/3/2017 0:36	62
14/3/2017 3:16	58	15/3/2017 4:21	60	16/3/2017 5:26	61	17/3/2017 6:31	60	18/3/2017 7:36	62	20/3/2017 0:41	63
14/3/2017 3:21	59	15/3/2017 4:26	59	16/3/2017 5:31	61	17/3/2017 6:36	60	18/3/2017 7:41	59	20/3/2017 0:46	62
14/3/2017 3:26	58	15/3/2017 4:31	61	16/3/2017 5:36	62	17/3/2017 6:41	61	18/3/2017 7:46	60	20/3/2017 0:51	62
14/3/2017 3:31	60	15/3/2017 4:36	60	16/3/2017 5:41	62	17/3/2017 6:46	62	18/3/2017 7:51	59	20/3/2017 0:56	62
14/3/2017 3:36	59	15/3/2017 4:41	61	16/3/2017 5:46	62	17/3/2017 6:51	62	18/3/2017 7:56	53	20/3/2017 1:01	61
14/3/2017 3:41	58	15/3/2017 4:46	60	16/3/2017 5:51	63	17/3/2017 6:56	61	19/3/2017 0:01	59	20/3/2017 1:06	62
14/3/2017 3:46	60	15/3/2017 4:51	61	16/3/2017 5:56	63	17/3/2017 7:01	60	19/3/2017 0:06	57	20/3/2017 1:11	62
14/3/2017 3:51	59	15/3/2017 4:56	61	16/3/2017 6:01	62	17/3/2017 7:06	64	19/3/2017 0:11	60	20/3/2017 1:16	61
14/3/2017 3:56	59	15/3/2017 5:01	61	16/3/2017 6:06	63	17/3/2017 7:11	61	19/3/2017 0:16	56	20/3/2017 1:21	61
14/3/2017 4:01	59	15/3/2017 5:06	61	16/3/2017 6:11	54	17/3/2017 7:16	61	19/3/2017 0:21	61	20/3/2017 1:26	61
14/3/2017 4:06	59	15/3/2017 5:11	61	16/3/2017 6:16	51	17/3/2017 7:21	61	19/3/2017 0:26	57	20/3/2017 1:31	61
14/3/2017 4:11	58	15/3/2017 5:16	60	16/3/2017 6:21	58	17/3/2017 7:26	60	19/3/2017 0:31			

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
20/3/2017 4:26	58	21/3/2017 5:31	61	22/3/2017 6:36	61	23/3/2017 23:41	57	25/3/2017 0:46	55	26/3/2017 1:51	62
20/3/2017 4:31	59	21/3/2017 5:36	61	22/3/2017 6:41	60	23/3/2017 23:46	58	25/3/2017 0:51	57	26/3/2017 1:56	63
20/3/2017 4:36	58	21/3/2017 5:41	61	22/3/2017 6:46	62	23/3/2017 23:51	53	25/3/2017 0:56	58	26/3/2017 2:01	62
20/3/2017 4:41	59	21/3/2017 5:46	61	22/3/2017 6:51	62	23/3/2017 23:56	59	25/3/2017 1:01	54	26/3/2017 2:06	63
20/3/2017 4:46	60	21/3/2017 5:51	62	22/3/2017 6:56	63	24/3/2017 0:01	51	25/3/2017 1:06	58	26/3/2017 2:11	62
20/3/2017 4:51	61	21/3/2017 5:56	62	22/3/2017 23:01	55	24/3/2017 0:06	54	25/3/2017 1:11	57	26/3/2017 2:16	62
20/3/2017 4:56	59	21/3/2017 6:01	62	22/3/2017 23:06	58	24/3/2017 0:11	53	25/3/2017 1:16	57	26/3/2017 2:21	62
20/3/2017 5:01	60	21/3/2017 6:06	62	22/3/2017 23:11	58	24/3/2017 0:16	55	25/3/2017 1:21	51	26/3/2017 2:26	62
20/3/2017 5:06	60	21/3/2017 6:11	42	22/3/2017 23:16	58	24/3/2017 0:21	52	25/3/2017 1:26	52	26/3/2017 2:31	61
20/3/2017 5:11	61	21/3/2017 6:16	44	22/3/2017 23:21	58	24/3/2017 0:26	63	25/3/2017 1:31	51	26/3/2017 2:36	62
20/3/2017 5:16	59	21/3/2017 6:21	58	22/3/2017 23:26	59	24/3/2017 0:31	53	25/3/2017 1:36	57	26/3/2017 2:41	61
20/3/2017 5:21	61	21/3/2017 6:26	58	22/3/2017 23:31	57	24/3/2017 0:36	63	25/3/2017 1:41	63	26/3/2017 2:46	62
20/3/2017 5:26	61	21/3/2017 6:31	61	22/3/2017 23:36	59	24/3/2017 0:41	60	25/3/2017 1:46	52	26/3/2017 2:51	62
20/3/2017 5:31	61	21/3/2017 6:36	60	22/3/2017 23:41	58	24/3/2017 0:46	63	25/3/2017 1:51	49	26/3/2017 2:56	62
20/3/2017 5:36	62	21/3/2017 6:41	62	22/3/2017 23:46	58	24/3/2017 0:51	46	25/3/2017 1:56	63	26/3/2017 3:01	61
20/3/2017 5:41	62	21/3/2017 6:46	62	22/3/2017 23:51	57	24/3/2017 0:56	63	25/3/2017 2:01	48	26/3/2017 3:06	62
20/3/2017 5:46	62	21/3/2017 6:51	63	22/3/2017 23:56	57	24/3/2017 1:01	63	25/3/2017 2:06	63	26/3/2017 3:11	61
20/3/2017 5:51	62	21/3/2017 6:56	64	23/3/2017 0:01	55	24/3/2017 1:06	47	25/3/2017 2:11	54	26/3/2017 3:16	61
20/3/2017 5:56	62	21/3/2017 23:01	57	23/3/2017 0:06	57	24/3/2017 1:11	63	25/3/2017 2:16	62	26/3/2017 3:21	61
20/3/2017 6:01	63	21/3/2017 23:06	59	23/3/2017 0:11	54	24/3/2017 1:16	63	25/3/2017 2:21	63	26/3/2017 3:26	61
20/3/2017 6:06	61	21/3/2017 23:11	59	23/3/2017 0:16	63	24/3/2017 1:21	63	25/3/2017 2:26	62	26/3/2017 3:31	61
20/3/2017 6:11	53	21/3/2017 23:16	60	23/3/2017 0:21	58	24/3/2017 1:26	63	25/3/2017 2:31	62	26/3/2017 3:36	60
20/3/2017 6:16	57	21/3/2017 23:21	59	23/3/2017 0:26	54	24/3/2017 1:31	63	25/3/2017 2:36	62	26/3/2017 3:41	61
20/3/2017 6:21	60	21/3/2017 23:26	58	23/3/2017 0:31	50	24/3/2017 1:36	62	25/3/2017 2:41	53	26/3/2017 3:46	63
20/3/2017 6:26	59	21/3/2017 23:31	59	23/3/2017 0:36	56	24/3/2017 1:41	61	25/3/2017 2:46	63	26/3/2017 3:51	61
20/3/2017 6:31	62	21/3/2017 23:36	57	23/3/2017 0:41	63	24/3/2017 1:46	62	25/3/2017 2:51	63	26/3/2017 3:56	62
20/3/2017 6:36	60	21/3/2017 23:41	58	23/3/2017 0:46	63	24/3/2017 1:51	60	25/3/2017 2:56	63	26/3/2017 4:01	61
20/3/2017 6:41	62	21/3/2017 23:46	59	23/3/2017 0:51	62	24/3/2017 1:56	61	25/3/2017 3:01	61	26/3/2017 4:06	61
20/3/2017 6:46	64	21/3/2017 23:51	57	23/3/2017 0:56	62	24/3/2017 2:01	61	25/3/2017 3:06	62	26/3/2017 4:11	62
20/3/2017 6:51	63	21/3/2017 23:56	57	23/3/2017 1:01	63	24/3/2017 2:06	60	25/3/2017 3:11	62	26/3/2017 4:16	61
20/3/2017 6:56	64	22/3/2017 0:01	53	23/3/2017 1:06	63	24/3/2017 2:11	61	25/3/2017 3:16	62	26/3/2017 4:21	61
20/3/2017 23:01	58	22/3/2017 0:06	53	23/3/2017 1:11	63	24/3/2017 2:16	60	25/3/2017 3:21	61	26/3/2017 4:26	60
20/3/2017 23:06	62	22/3/2017 0:11	51	23/3/2017 1:16	61	24/3/2017 2:21	60	25/3/2017 3:26	61	26/3/2017 4:31	61
20/3/2017 23:11	60	22/3/2017 0:16	57	23/3/2017 1:21	62	24/3/2017 2:26	61	25/3/2017 3:31	62	26/3/2017 4:36	60
20/3/2017 23:16	60	22/3/2017 0:21	49	23/3/2017 1:26	61	24/3/2017 2:31	61	25/3/2017 3:36	62	26/3/2017 4:41	61
20/3/2017 23:21	59	22/3/2017 0:26	56	23/3/2017 1:31	61	24/3/2017 2:36	61	25/3/2017 3:41	62	26/3/2017 4:46	60
20/3/2017 23:26	58	22/3/2017 0:31	55	23/3/2017 1:36	62	24/3/2017 2:41	60	25/3/2017 3:46	62	26/3/2017 4:51	62
20/3/2017 23:31	59	22/3/2017 0:36	63	23/3/2017 1:41	62	24/3/2017 2:46	59	25/3/2017 3:51	62	26/3/2017 4:56	61
20/3/2017 23:36	55	22/3/2017 0:41	62	23/3/2017 1:46	61	24/3/2017 2:51	59	25/3/2017 3:56	62	26/3/2017 5:01	61
20/3/2017 23:41	57	22/3/2017 0:46	62	23/3/2017 1:51	62	24/3/2017 2:56	59	25/3/2017 4:01	61	26/3/2017 5:06	59
20/3/2017 23:46	54	22/3/2017 0:51	62	23/3/2017 1:56	62	24/3/2017 3:01	60	25/3/2017 4:06	62	26/3/2017 5:11	60
20/3/2017 23:51	48	22/3/2017 0:56	62	23/3/2017 2:01	61	24/3/2017 3:06	59	25/3/2017 4:11	61	26/3/2017 5:16	61
20/3/2017 23:56	58	22/3/2017 1:01	63	23/3/2017 2:06	60	24/3/2017 3:11	59	25/3/2017 4:16	61	26/3/2017 5:21	60
21/3/2017 0:01	63	22/3/2017 1:06	63	23/3/2017 2:11	61	24/3/2017 3:16	59	25/3/2017 4:21	62	26/3/2017 5:26	61
21/3/2017 0:06	53	22/3/2017 1:11	62	23/3/2017 2:16	61	24/3/2017 3:21	59	25/3/2017 4:26	61	26/3/2017 5:31	61
21/3/2017 0:11	54	22/3/2017 1:16	53	23/3/2017 2:21	61	24/3/2017 3:26	59	25/3/2017 4:31	61	26/3/2017 5:36	62
21/3/2017 0:16	63	22/3/2017 1:21	62	23/3/2017 2:26	61	24/3/2017 3:31	60	25/3/2017 4:36	60	26/3/2017 5:41	61
21/3/2017 0:21	56	22/3/2017 1:26	62	23/3/2017 2:31	61	24/3/2017 3:36	60	25/3/2017 4:41	61	26/3/2017 5:46	62
21/3/2017 0:26	56	22/3/2017 1:31	61	23/3/2017 2:36	61	24/3/2017 3:41	60	25/3/2017 4:46	60	26/3/2017 5:51	61
21/3/2017 0:31	63	22/3/2017 1:36	62	23/3/2017 2:41	61	24/3/2017 3:46	59	25/3/2017 4:51	60	26/3/2017 5:56	62
21/3/2017 0:36	51	22/3/2017 1:41	62	23/3/2017 2:46	60	24/3/2017 3:51	60	25/3/2017 4:56	61	26/3/2017 6:01	61
21/3/2017 0:41	63	22/3/2017 1:46	62	23/3/2017 2:51	60	24/3/2017 3:56	61	25/3/2017 5:01	61	26/3/2017 6:06	62
21/3/2017 0:46	63	22/3/2017 1:51	61	23/3/2017 2:56	60	24/3/2017 4:01	59	25/3/2017 5:06	62	26/3/2017 6:11	62
21/3/2017 0:51	49	22/3/2017 1:56	60	23/3/2017 3:01	60	24/3/2017 4:06	60	25/3/2017 5:11	61	26/3/2017 6:16	53
21/3/2017 0:56	62	22/3/2017 2:01	61	23/3/2017 3:06	62	24/3/2017 4:11	59	25/3/2017 5:16	60	26/3/2017 6:21	63
21/3/2017 1:01	63	22/3/2017 2:06	60	23/3/2017 3:11	60	24/3/2017 4:16	60	25/3/2017 5:21	61	26/3/2017 6:26	53
21/3/2017 1:06	63	22/3/2017 2:11	61	23/3/2017 3:16	60	24/3/2017 4:21	59	25/3/2017 5:26	61	26/3/2017 6:31	58
21/3/2017 1:11	56	22/3/2017 2:16	59	23/3/2017 3:21	59	24/3/2017 4:26	60	25/3/2017 5:31	61	26/3/2017 6:36	48
21/3/2017 1:16	63	22/3/2017 2:21	60	23/3/2017 3:26	59	24/3/2017 4:31	59	25/3/2017 5:36	62	26/3/2017 6:41	61
21/3/2017 1:21	62	22/3/2017 2:26	59	23/3/2017 3:31	59	24/3/2017 4:36	58	25/3/2017 5:41	62	26/3/2017 6:46	55
21/3/2017 1:26	62	22/3/2017 2:31	61	23/3/2017 3:36	60	24/3/2017 4:41	59	25/3/2017 5:46	62	26/3/2017 6:51	57
21/3/2017 1:31	62	22/3/2017 2:36	61	23/3/2017 3:41	60	24/3/2017 4:46	59	25/3/2017 5:51	62	26/3/2017 6:56	58
21/3/2017 1:36	62	22/3/2017 2:41	60	23/3/2017 3:46	60	24/3/2017 4:51	60	25/3/2017 5:56	62	26/3/2017 23:01	59
21/3/2017 1:41	63	22/3/2017 2:46	60	23/3/2017 3:51	60	24/3/2017 4:56	60	25/3/2017 6:01	62	26/3/2017 23:06	59
21/3/2017 1:46	62	22/3/2017 2:51	60	23/3/2017 3:56	61	24/3/2017 5:01	60	25/3/2017 6:06	62	26/3/2017 23:11	55
21/3/2017 1:51	60	22/3/2017 2:56	59	23/3/2017 4:01	58	24/3/2017 5:06	60	25/3/2017 6:11	62	26/3/2017 23:16	59
21/3/2017 1:56	60	22/3/2017 3:01	59	23/3/2017 4:06	60	24/3/2017 5:11	59	25/3/2017 6:16	63	26/3/2017 23:21	58
21/3/2017 2:01	60	22/3/2017 3:06	60	23/3/2017 4:11	60	24/3/2017 5:16	61	25/3/2017 6:21	51	26/3/2017 23:26	58
21/3/2017 2:06	61	22/3/2017 3:11	59	23/3/2017 4:16	60	24/3/2017 5:21	60	25/3/2017 6:26	55	26/3/2017 23:31	54
21/3/2017 2:11	60	22/3/2017 3:16	59	23/3/2017 4:21	59	24/3/2017 5:26	61	25/3/2017 6:31	56	26/3/2017 23:36	50
21/3/2017 2:16	60	22/3/2017 3:21	61	23/3/2017 4:26	59	24/3/2017 5:31	61	25/3/2017 6:36	52	26/3/2017 23:41	56
21/3/2017 2:21	61	22/3/2017 3:26	60	23/3/2017 4:31	61	24/3/2017 5:36	61	25/3/2017 6:41	61	26/3/2017 23:46	53
21/3/2017 2:26	60	22/3/2017 3:31	59	23/3/2017 4:36	59	24/3/2017 5:41	60	25/3/2017 6:46	57	26/3/2017 23:51	59
21/3/2017 2:31	61	22/3/2017 3:36	59	23/3/2017 4:41	59	24/3/2017 5:46	61	25/3/2017 6:51	62	26/3/2017 23:56	63
21/3/2017 2:36	60	22/3/2017 3:41	60	23/3/2017 4:46	59	24/3/2017 5:51	62	25/3/2017 6:56	61		
21/3/2017 2:41	60	22/3/2017 3:46	59	23/3/2017 4:51	59	24/3/2017 5:56	63	25/3			

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
Normal Day 07:00-19:00											
27/2/2017 7:01	61	3/3/2017 13:01	64	9/3/2017 7:31	61	14/3/2017 14:01	64	20/3/2017 8:31	62	24/3/2017 15:01	66
27/2/2017 7:31	62	3/3/2017 13:31	64	9/3/2017 8:01	62	14/3/2017 14:31	64	20/3/2017 9:01	63	24/3/2017 15:31	64
27/2/2017 8:01	61	3/3/2017 14:01	67	9/3/2017 8:31	64	14/3/2017 15:01	65	20/3/2017 9:31	64	24/3/2017 16:01	64
27/2/2017 8:31	63	3/3/2017 14:31	65	9/3/2017 9:01	65	14/3/2017 15:31	64	20/3/2017 10:01	65	24/3/2017 16:31	65
27/2/2017 9:01	63	3/3/2017 15:01	63	9/3/2017 9:31	67	14/3/2017 16:01	65	20/3/2017 10:31	65	24/3/2017 17:01	64
27/2/2017 9:31	64	3/3/2017 15:31	65	9/3/2017 10:01	68	14/3/2017 16:31	64	20/3/2017 11:01	65	24/3/2017 17:31	61
27/2/2017 10:01	64	3/3/2017 16:01	65	9/3/2017 10:31	66	14/3/2017 17:01	62	20/3/2017 11:31	62	24/3/2017 18:01	61
27/2/2017 10:31	64	3/3/2017 16:31	65	9/3/2017 11:01	66	14/3/2017 17:31	61	20/3/2017 12:01	62	24/3/2017 18:31	60
27/2/2017 11:01	64	3/3/2017 17:01	64	9/3/2017 11:31	65	14/3/2017 18:01	61	20/3/2017 12:31	62	25/3/2017 7:01	60
27/2/2017 11:31	64	3/3/2017 17:31	64	9/3/2017 12:01	62	14/3/2017 18:31	60	20/3/2017 13:01	64	25/3/2017 7:31	61
27/2/2017 12:01	61	3/3/2017 18:01	62	9/3/2017 12:31	62	15/3/2017 7:01	61	20/3/2017 13:31	64	25/3/2017 8:01	62
27/2/2017 12:31	63	3/3/2017 18:31	62	9/3/2017 13:01	64	15/3/2017 7:31	61	20/3/2017 14:01	63	25/3/2017 8:31	62
27/2/2017 13:01	64	4/3/2017 7:01	60	9/3/2017 13:31	65	15/3/2017 8:01	61	20/3/2017 14:31	64	25/3/2017 9:01	64
27/2/2017 13:31	65	4/3/2017 7:31	61	9/3/2017 14:01	63	15/3/2017 8:31	62	20/3/2017 15:01	63	25/3/2017 9:31	65
27/2/2017 14:01	66	4/3/2017 8:01	63	9/3/2017 14:31	63	15/3/2017 9:01	63	20/3/2017 15:31	65	25/3/2017 10:01	64
27/2/2017 14:31	64	4/3/2017 8:31	66	9/3/2017 15:01	63	15/3/2017 9:31	64	20/3/2017 16:01	65	25/3/2017 10:31	64
27/2/2017 15:01	64	4/3/2017 9:01	67	9/3/2017 15:31	64	15/3/2017 10:01	65	20/3/2017 16:31	66	25/3/2017 11:01	63
27/2/2017 15:31	64	4/3/2017 9:31	67	9/3/2017 16:01	65	15/3/2017 10:31	64	20/3/2017 17:01	65	25/3/2017 11:31	65
27/2/2017 16:01	64	4/3/2017 10:01	68	9/3/2017 16:31	64	15/3/2017 11:01	65	20/3/2017 17:31	62	25/3/2017 12:01	65
27/2/2017 16:31	64	4/3/2017 10:31	65	9/3/2017 17:01	63	15/3/2017 11:31	62	20/3/2017 18:01	61	25/3/2017 12:31	65
27/2/2017 17:01	63	4/3/2017 11:01	68	9/3/2017 17:31	62	15/3/2017 12:01	61	20/3/2017 18:31	59	25/3/2017 13:01	66
27/2/2017 17:31	61	4/3/2017 11:31	61	9/3/2017 18:01	61	15/3/2017 12:31	63	21/3/2017 7:01	61	25/3/2017 13:31	64
27/2/2017 18:01	62	4/3/2017 12:01	61	9/3/2017 18:31	61	15/3/2017 13:01	64	21/3/2017 7:31	61	25/3/2017 14:01	64
27/2/2017 18:31	62	4/3/2017 12:31	61	10/3/2017 7:01	60	15/3/2017 13:31	66	21/3/2017 8:01	63	25/3/2017 14:31	64
28/2/2017 7:01	60	4/3/2017 13:01	62	10/3/2017 7:31	60	15/3/2017 14:01	65	21/3/2017 8:31	67	25/3/2017 15:01	63
28/2/2017 7:31	61	4/3/2017 13:31	53	10/3/2017 8:01	62	15/3/2017 14:31	64	21/3/2017 9:01	67	25/3/2017 15:31	63
28/2/2017 8:01	62	4/3/2017 14:01	64	10/3/2017 8:31	64	15/3/2017 15:01	64	21/3/2017 9:31	65	25/3/2017 16:01	63
28/2/2017 8:31	63	4/3/2017 14:31	62	10/3/2017 9:01	65	15/3/2017 15:31	64	21/3/2017 10:01	67	25/3/2017 16:31	63
28/2/2017 9:01	65	4/3/2017 15:01	67	10/3/2017 9:31	66	15/3/2017 16:01	65	21/3/2017 10:31	65	25/3/2017 17:01	62
28/2/2017 9:31	67	4/3/2017 15:31	68	10/3/2017 10:01	66	15/3/2017 16:31	65	21/3/2017 11:01	65	25/3/2017 17:31	61
28/2/2017 10:01	66	4/3/2017 16:01	68	10/3/2017 10:31	66	15/3/2017 17:01	64	21/3/2017 11:31	63	25/3/2017 18:01	61
28/2/2017 10:31	68	4/3/2017 16:31	65	10/3/2017 11:01	67	15/3/2017 17:31	62	21/3/2017 12:01	61	25/3/2017 18:31	61
28/2/2017 11:01	67	4/3/2017 17:01	64	10/3/2017 11:31	63	15/3/2017 18:01	62	21/3/2017 12:31	63		
28/2/2017 11:31	63	4/3/2017 17:31	64	10/3/2017 12:01	63	15/3/2017 18:31	62	21/3/2017 13:01	65	Normal Day 19:00-23:00 Sunday & Holiday 07:00-23:00	
28/2/2017 12:01	63	4/3/2017 18:01	62	10/3/2017 12:31	61	16/3/2017 7:01	60	21/3/2017 13:31	64		
28/2/2017 12:31	62	4/3/2017 18:31	61	10/3/2017 13:01	65	16/3/2017 7:31	61	21/3/2017 14:01	64	27/2/2017 19:01	62
28/2/2017 13:01	65	6/3/2017 7:01	60	10/3/2017 13:31	65	16/3/2017 8:01	62	21/3/2017 14:31	64	27/2/2017 19:06	61
28/2/2017 13:31	65	6/3/2017 7:31	62	10/3/2017 14:01	65	16/3/2017 8:31	63	21/3/2017 15:01	64	27/2/2017 19:11	61
28/2/2017 14:01	64	6/3/2017 8:01	62	10/3/2017 14:31	65	16/3/2017 9:01	64	21/3/2017 15:31	64	27/2/2017 19:16	61
28/2/2017 14:31	64	6/3/2017 8:31	63	10/3/2017 15:01	65	16/3/2017 9:31	66	21/3/2017 16:01	64	27/2/2017 19:21	62
28/2/2017 15:01	63	6/3/2017 9:01	65	10/3/2017 15:31	65	16/3/2017 10:01	66	21/3/2017 16:31	64	27/2/2017 19:26	61
28/2/2017 15:31	64	6/3/2017 9:31	65	10/3/2017 16:01	66	16/3/2017 10:31	65	21/3/2017 17:01	63	27/2/2017 19:31	62
28/2/2017 16:01	64	6/3/2017 10:01	66	10/3/2017 16:31	65	16/3/2017 11:01	66	21/3/2017 17:31	61	27/2/2017 19:36	61
28/2/2017 16:31	62	6/3/2017 10:31	65	10/3/2017 17:01	63	16/3/2017 11:31	63	21/3/2017 18:01	60	27/2/2017 19:41	61
28/2/2017 17:01	62	6/3/2017 11:01	67	10/3/2017 17:31	61	16/3/2017 12:01	64	21/3/2017 18:31	61	27/2/2017 19:46	61
28/2/2017 17:31	61	6/3/2017 11:31	66	10/3/2017 18:01	60	16/3/2017 12:31	62	22/3/2017 7:01	60	27/2/2017 19:51	62
28/2/2017 18:01	61	6/3/2017 12:01	63	10/3/2017 18:31	61	16/3/2017 13:01	65	22/3/2017 7:31	59	27/2/2017 19:56	60
28/2/2017 18:31	62	6/3/2017 12:31	63	11/3/2017 7:01	60	16/3/2017 13:31	65	22/3/2017 8:01	63	27/2/2017 20:01	60
1/3/2017 7:01	60	6/3/2017 13:01	64	11/3/2017 7:31	61	16/3/2017 14:01	65	22/3/2017 8:31	64	27/2/2017 20:06	60
1/3/2017 7:31	61	6/3/2017 13:31	67	11/3/2017 8:01	62	16/3/2017 14:31	65	22/3/2017 9:01	64	27/2/2017 20:11	61
1/3/2017 8:01	61	6/3/2017 14:01	66	11/3/2017 8:31	62	16/3/2017 15:01	65	22/3/2017 9:31	65	27/2/2017 20:16	60
1/3/2017 8:31	64	6/3/2017 14:31	66	11/3/2017 9:01	64	16/3/2017 15:31	65	22/3/2017 10:01	67	27/2/2017 20:21	61
1/3/2017 9:01	63	6/3/2017 15:01	65	11/3/2017 9:31	65	16/3/2017 16:01	64	22/3/2017 10:31	67	27/2/2017 20:26	61
1/3/2017 9:31	63	6/3/2017 15:31	66	11/3/2017 10:01	67	16/3/2017 16:31	64	22/3/2017 11:01	65	27/2/2017 20:31	61
1/3/2017 10:01	64	6/3/2017 16:01	66	11/3/2017 10:31	64	16/3/2017 17:01	62	22/3/2017 11:31	62	27/2/2017 20:36	61
1/3/2017 10:31	63	6/3/2017 16:31	65	11/3/2017 11:01	64	16/3/2017 17:31	61	22/3/2017 12:01	60	27/2/2017 20:41	62
1/3/2017 11:01	63	6/3/2017 17:01	64	11/3/2017 11:31	62	16/3/2017 18:01	62	22/3/2017 12:31	60	27/2/2017 20:46	62
1/3/2017 11:31	62	6/3/2017 17:31	63	11/3/2017 12:01	60	16/3/2017 18:31	61	22/3/2017 13:01	64	27/2/2017 20:51	60
1/3/2017 12:01	62	6/3/2017 18:01	62	11/3/2017 12:31	60	17/3/2017 7:01	60	22/3/2017 13:31	64	27/2/2017 20:56	60
1/3/2017 12:31	63	6/3/2017 18:31	62	11/3/2017 13:01	64	17/3/2017 7:31	60	22/3/2017 14:01	65	27/2/2017 21:01	60
1/3/2017 13:01	64	7/3/2017 7:01	60	11/3/2017 13:31	67	17/3/2017 8:01	60	22/3/2017 14:31	65	27/2/2017 21:06	59
1/3/2017 13:31	64	7/3/2017 7:31	61	11/3/2017 14:01	63	17/3/2017 8:31	61	22/3/2017 15:01	65	27/2/2017 21:11	60
1/3/2017 14:01	64	7/3/2017 8:01	62	11/3/2017 14:31	67	17/3/2017 9:01	63	22/3/2017 15:31	67	27/2/2017 21:16	60
1/3/2017 14:31	64	7/3/2017 8:31	67	11/3/2017 15:01	65	17/3/2017 9:31	65	22/3/2017 16:01	66	27/2/2017 21:21	59
1/3/2017 15:01	65	7/3/2017 9:01	67	11/3/2017 15:31	63	17/3/2017 10:01	65	22/3/2017 16:31	65	27/2/2017 21:26	60
1/3/2017 15:31	65	7/3/2017 9:31	63	11/3/2017 16:01	64	17/3/2017 10:31	65	22/3/2017 17:01	63	27/2/2017 21:31	60
1/3/2017 16:01	65	7/3/2017 10:01	68	11/3/2017 16:31	66	17/3/2017 11:01	63	22/3/2017 17:31	62	27/2/2017 21:36	59
1/3/2017 16:31	65	7/3/2017 10:31	67	11/3/2017 17:01	63	17/3/2017 11:31	63	22/3/2017 18:01	60	27/2/2017 21:41	60
1/3/2017 17:01	63	7/3/2017 11:01	66	11/3/2017 17:31	62	17/3/2017 12:01	61	22/3/2017 18:31	61	27/2/2017 21:46	60
1/3/2017 17:31	62	7/3/2017 11:31	64	11/3/2017 18:01	61	17/3/2017 12:31	62	23/3/2017 7:01	61	27/2/2017 21:51	60
2/3/2017 7:01	60	7/3/2017 12:01	63	11/3/2017 18:31	60	17/3/2017 13:01	63	23/3/2017 7:31	61	27/2/2017 21:56	60
2/3/2017 7:31	61	7/3/2017 12:31	63	13/3/2017 7:01	60	17/3/2017 13:31	65	23/3/2017 8:01	62	27/2/2017 22:01	60
2/3/2017 8:01	62	7/3/2017 13:01	66	13/3/2017 7:31	61	17/3/2017 14:01	65	23/3/2017 8:31	64	27/2/2017 22:06	60
2/3/2017 8:31	62	7/3/2017 13:31	65	13/3/2017 8:01	63	17/3/2017 14:31	65	23/3/2017 9:01	65	27/2/2017 22:11	60
2/											

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)											
28/2/2017 21:01	62	2/3/2017 22:06	62	5/3/2017 7:11	58	5/3/2017 16:16	54	6/3/2017 21:21	60	8/3/2017 22:26	61		
28/2/2017 21:06	60	2/3/2017 22:11	62	5/3/2017 7:16	58	5/3/2017 16:21	56	6/3/2017 21:26	60	8/3/2017 22:31	61		
28/2/2017 21:11	60	2/3/2017 22:16	62	5/3/2017 7:21	62	5/3/2017 16:26	55	6/3/2017 21:31	59	8/3/2017 22:36	61		
28/2/2017 21:16	61	2/3/2017 22:21	62	5/3/2017 7:26	62	5/3/2017 16:31	55	6/3/2017 21:36	59	8/3/2017 22:41	60		
28/2/2017 21:21	61	2/3/2017 22:26	62	5/3/2017 7:31	59	5/3/2017 16:36	56	6/3/2017 21:41	59	8/3/2017 22:46	61		
28/2/2017 21:26	60	2/3/2017 22:31	62	5/3/2017 7:36	60	5/3/2017 16:41	55	6/3/2017 21:46	59	8/3/2017 22:51	60		
28/2/2017 21:31	60	2/3/2017 22:36	62	5/3/2017 7:41	61	5/3/2017 16:46	57	6/3/2017 21:51	59	8/3/2017 22:56	60		
28/2/2017 21:36	63	2/3/2017 22:41	62	5/3/2017 7:46	60	5/3/2017 16:51	56	6/3/2017 21:56	60	9/3/2017 19:01	60		
28/2/2017 21:41	61	2/3/2017 22:46	61	5/3/2017 7:51	59	5/3/2017 16:56	56	6/3/2017 22:01	60	9/3/2017 19:06	61		
28/2/2017 21:46	60	2/3/2017 22:51	62	5/3/2017 7:56	60	5/3/2017 17:01	55	6/3/2017 22:06	59	9/3/2017 19:11	61		
28/2/2017 21:51	62	2/3/2017 22:56	61	5/3/2017 8:01	61	5/3/2017 17:06	53	6/3/2017 22:11	59	9/3/2017 19:16	62		
28/2/2017 21:56	61	3/3/2017 19:01	63	5/3/2017 8:06	60	5/3/2017 17:11	55	6/3/2017 22:16	61	9/3/2017 19:21	62		
28/2/2017 22:01	61	3/3/2017 19:06	59	5/3/2017 8:11	60	5/3/2017 17:16	58	6/3/2017 22:21	60	9/3/2017 19:26	63		
28/2/2017 22:06	60	3/3/2017 19:11	56	5/3/2017 8:16	60	5/3/2017 17:21	63	6/3/2017 22:26	60	9/3/2017 19:31	62		
28/2/2017 22:11	60	3/3/2017 19:16	63	5/3/2017 8:21	60	5/3/2017 17:26	60	6/3/2017 22:31	60	9/3/2017 19:36	61		
28/2/2017 22:16	62	3/3/2017 19:21	63	5/3/2017 8:26	61	5/3/2017 17:31	61	6/3/2017 22:36	61	9/3/2017 19:41	62		
28/2/2017 22:21	60	3/3/2017 19:26	63	5/3/2017 8:31	61	5/3/2017 17:36	56	6/3/2017 22:41	59	9/3/2017 19:46	61		
28/2/2017 22:26	63	3/3/2017 19:31	63	5/3/2017 8:36	60	5/3/2017 17:41	56	6/3/2017 22:46	59	9/3/2017 19:51	62		
28/2/2017 22:31	60	3/3/2017 19:36	63	5/3/2017 8:41	60	5/3/2017 17:46	58	6/3/2017 22:51	59	9/3/2017 19:56	61		
28/2/2017 22:36	60	3/3/2017 19:41	63	5/3/2017 8:46	61	5/3/2017 17:51	55	6/3/2017 22:56	60	9/3/2017 20:01	62		
28/2/2017 22:41	60	3/3/2017 19:46	63	5/3/2017 8:51	61	5/3/2017 17:56	51	7/3/2017 19:01	59	9/3/2017 20:06	60		
28/2/2017 22:46	61	3/3/2017 19:51	40	5/3/2017 8:56	61	5/3/2017 18:01	61	7/3/2017 19:06	60	9/3/2017 20:11	61		
28/2/2017 22:51	60	3/3/2017 19:56	63	5/3/2017 9:01	61	5/3/2017 18:06	61	7/3/2017 19:11	60	9/3/2017 20:16	61		
28/2/2017 22:56	60	3/3/2017 20:01	63	5/3/2017 9:06	60	5/3/2017 18:11	61	7/3/2017 19:16	61	9/3/2017 20:21	61		
1/3/2017 19:01	61	3/3/2017 20:06	61	5/3/2017 9:11	61	5/3/2017 18:16	61	7/3/2017 19:21	61	9/3/2017 20:26	60		
1/3/2017 19:06	61	3/3/2017 20:11	63	5/3/2017 9:16	61	5/3/2017 18:21	61	7/3/2017 19:26	61	9/3/2017 20:31	60		
1/3/2017 19:11	60	3/3/2017 20:16	62	5/3/2017 9:21	61	5/3/2017 18:26	60	7/3/2017 19:31	62	9/3/2017 20:36	60		
1/3/2017 19:16	60	3/3/2017 20:21	62	5/3/2017 9:26	61	5/3/2017 18:31	61	7/3/2017 19:36	61	9/3/2017 20:41	61		
1/3/2017 19:21	60	3/3/2017 20:26	61	5/3/2017 9:31	61	5/3/2017 18:36	60	7/3/2017 19:41	63	9/3/2017 20:46	60		
1/3/2017 19:26	61	3/3/2017 20:31	61	5/3/2017 9:36	61	5/3/2017 18:41	61	7/3/2017 19:46	62	9/3/2017 20:51	60		
1/3/2017 19:31	61	3/3/2017 20:36	61	5/3/2017 9:41	60	5/3/2017 18:46	60	7/3/2017 19:51	58	9/3/2017 20:56	61		
1/3/2017 19:36	61	3/3/2017 20:41	61	5/3/2017 9:46	60	5/3/2017 18:51	60	7/3/2017 19:56	54	9/3/2017 21:01	60		
1/3/2017 19:41	62	3/3/2017 20:46	63	5/3/2017 9:51	60	5/3/2017 18:56	60	7/3/2017 20:01	62	9/3/2017 21:06	60		
1/3/2017 19:46	61	3/3/2017 20:51	61	5/3/2017 9:56	61	5/3/2017 19:01	60	7/3/2017 20:06	62	9/3/2017 21:11	60		
1/3/2017 19:51	61	3/3/2017 20:56	60	5/3/2017 10:01	62	5/3/2017 19:06	59	7/3/2017 20:11	61	9/3/2017 21:16	60		
1/3/2017 19:56	60	3/3/2017 21:01	61	5/3/2017 10:06	61	5/3/2017 19:11	60	7/3/2017 20:16	61	9/3/2017 21:21	60		
1/3/2017 20:01	61	3/3/2017 21:06	61	5/3/2017 10:11	61	5/3/2017 19:16	60	7/3/2017 20:21	61	9/3/2017 21:26	60		
1/3/2017 20:06	60	3/3/2017 21:11	62	5/3/2017 10:16	62	5/3/2017 19:21	59	7/3/2017 20:26	56	9/3/2017 21:31	60		
1/3/2017 20:11	60	3/3/2017 21:16	53	5/3/2017 10:21	61	5/3/2017 19:26	60	7/3/2017 20:31	57	9/3/2017 21:36	60		
1/3/2017 20:16	60	3/3/2017 21:21	60	5/3/2017 10:26	61	5/3/2017 19:31	60	7/3/2017 20:36	61	9/3/2017 21:41	60		
1/3/2017 20:21	60	3/3/2017 21:26	61	5/3/2017 10:31	58	5/3/2017 19:36	60	7/3/2017 20:41	61	9/3/2017 21:46	60		
1/3/2017 20:26	60	3/3/2017 21:31	61	5/3/2017 10:36	57	5/3/2017 19:41	59	7/3/2017 20:46	61	9/3/2017 21:51	59		
1/3/2017 20:31	60	3/3/2017 21:36	62	5/3/2017 10:41	58	5/3/2017 19:46	59	7/3/2017 20:51	60	9/3/2017 21:56	59		
1/3/2017 20:36	60	3/3/2017 21:41	61	5/3/2017 10:46	60	5/3/2017 19:51	60	7/3/2017 20:56	61	9/3/2017 22:01	59		
1/3/2017 20:41	60	3/3/2017 21:46	62	5/3/2017 10:51	61	5/3/2017 19:56	59	7/3/2017 21:01	63	9/3/2017 22:06	59		
1/3/2017 20:46	59	3/3/2017 21:51	55	5/3/2017 10:56	60	5/3/2017 20:01	59	7/3/2017 21:06	56	9/3/2017 22:11	59		
1/3/2017 20:51	61	3/3/2017 21:56	63	5/3/2017 11:01	61	5/3/2017 20:06	60	7/3/2017 21:11	63	9/3/2017 22:16	59		
1/3/2017 20:56	60	3/3/2017 22:01	59	5/3/2017 11:06	63	5/3/2017 20:11	59	7/3/2017 21:16	60	9/3/2017 22:21	61		
1/3/2017 21:01	60	3/3/2017 22:06	60	5/3/2017 11:11	56	5/3/2017 20:16	60	7/3/2017 21:21	61	9/3/2017 22:26	60		
1/3/2017 21:06	59	3/3/2017 22:11	61	5/3/2017 11:16	58	5/3/2017 20:21	59	7/3/2017 21:26	61	9/3/2017 22:31	59		
1/3/2017 21:11	60	3/3/2017 22:16	61	5/3/2017 11:21	58	5/3/2017 20:26	59	7/3/2017 21:31	60	9/3/2017 22:36	59		
1/3/2017 21:16	60	3/3/2017 22:21	60	5/3/2017 11:26	61	5/3/2017 20:31	59	7/3/2017 21:36	60	9/3/2017 22:41	58		
1/3/2017 21:21	60	3/3/2017 22:26	60	5/3/2017 11:31	61	5/3/2017 20:36	59	7/3/2017 21:41	54	9/3/2017 22:46	59		
1/3/2017 21:26	59	3/3/2017 22:31	60	5/3/2017 11:36	60	5/3/2017 20:41	59	7/3/2017 21:46	55	9/3/2017 22:51	60		
1/3/2017 21:31	60	3/3/2017 22:36	61	5/3/2017 11:41	62	5/3/2017 20:46	60	7/3/2017 21:51	60	9/3/2017 22:56	60		
1/3/2017 21:36	60	3/3/2017 22:41	61	5/3/2017 11:46	60	5/3/2017 20:51	58	7/3/2017 21:56	60	10/3/2017 19:01	62		
1/3/2017 21:41	60	3/3/2017 22:46	60	5/3/2017 11:51	59	5/3/2017 20:56	59	7/3/2017 22:01	60	10/3/2017 19:06	58		
1/3/2017 21:46	60	3/3/2017 22:51	50	5/3/2017 11:56	54	5/3/2017 21:01	59	7/3/2017 22:06	60	10/3/2017 19:11	60		
1/3/2017 21:51	59	3/3/2017 22:56	60	5/3/2017 12:01	63	5/3/2017 21:06	60	7/3/2017 22:11	60	10/3/2017 19:16	61		
1/3/2017 21:56	59	4/3/2017 19:01	62	5/3/2017 12:06	60	5/3/2017 21:11	59	7/3/2017 22:16	60	10/3/2017 19:21	61		
1/3/2017 22:01	60	4/3/2017 19:06	61	5/3/2017 12:11	61	5/3/2017 21:16	59	7/3/2017 22:21	62	10/3/2017 19:26	61		
1/3/2017 22:06	60	4/3/2017 19:11	62	5/3/2017 12:16	61	5/3/2017 21:21	60	7/3/2017 22:26	63	10/3/2017 19:31	61		
1/3/2017 22:11	61	4/3/2017 19:16	62	5/3/2017 12:21	64	5/3/2017 21:26	59	7/3/2017 22:31	59	10/3/2017 19:36	61		
1/3/2017 22:16	60	4/3/2017 19:21	62	5/3/2017 12:26	54	5/3/2017 21:31	59	7/3/2017 22:36	61	10/3/2017 19:41	62		
1/3/2017 22:21	61	4/3/2017 19:26	61	5/3/2017 12:31	51	5/3/2017 21:36	59	7/3/2017 22:41	61	10/3/2017 19:46	61		
1/3/2017 22:26	59	4/3/2017 19:31	62	5/3/2017 12:36	63	5/3/2017 21:41	59	7/3/2017 22:46	63	10/3/2017 19:51	61		
1/3/2017 22:31	63	4/3/2017 19:36	62	5/3/2017 12:41	61	5/3/2017 21:46	59	7/3/2017 22:51	59	10/3/2017 19:56	61		
1/3/2017 22:36	60	4/3/2017 19:41	62	5/3/2017 12:46	61	5/3/2017 21:51	59	7/3/2017 22:56	59	10/3/2017 20:01	61		
1/3/2017 22:41	60	4/3/2017 19:46	62	5/3/2017 12:51	61	5/3/2017 21:56	59	8/3/2017 19:01	53	10/3/2017 20:06	61		
1/3/2017 22:46	59	4/3/2017 19:51	61	5/3/2017 12:56	62	5/3/2017 22:01	58	8/3/2017 19:06	61	10/3/2017 20:11	61		
1/3/2017 22:51	60	4/3/2017 19:56	61	5/3/2017 13:01	61	5/3/2017 22:06	59	8/3/2017 19:11	62	10/3/2017 20:16	63		
1/3/2017 22:56	60	4/3/2017 20:01	63	5/3/2017 13:06	62	5/3/2017 22:11	59	8/3/2017 19:16	62	10/3/2017 20:21	58		
2/													

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
11/3/2017 19:31	61	12/3/2017 12:36	60	12/3/2017 21:41	59	14/3/2017 22:46	60	17/3/2017 19:51	50	19/3/2017 8:56	61
11/3/2017 19:36	61	12/3/2017 12:41	61	12/3/2017 21:46	59	14/3/2017 22:51	59	17/3/2017 19:56	61	19/3/2017 9:01	61
11/3/2017 19:41	60	12/3/2017 12:46	62	12/3/2017 21:51	60	14/3/2017 22:56	60	17/3/2017 20:01	61	19/3/2017 9:06	60
11/3/2017 19:46	61	12/3/2017 12:51	61	12/3/2017 21:56	59	15/3/2017 19:01	61	17/3/2017 20:06	61	19/3/2017 9:11	62
11/3/2017 19:51	60	12/3/2017 12:56	61	12/3/2017 22:01	60	15/3/2017 19:06	60	17/3/2017 20:11	63	19/3/2017 9:16	61
11/3/2017 19:56	61	12/3/2017 13:01	61	12/3/2017 22:06	60	15/3/2017 19:11	61	17/3/2017 20:16	61	19/3/2017 9:21	61
11/3/2017 20:01	61	12/3/2017 13:06	60	12/3/2017 22:11	60	15/3/2017 19:16	61	17/3/2017 20:21	61	19/3/2017 9:26	60
11/3/2017 20:06	61	12/3/2017 13:11	60	12/3/2017 22:16	60	15/3/2017 19:21	61	17/3/2017 20:26	61	19/3/2017 9:31	61
11/3/2017 20:11	60	12/3/2017 13:16	60	12/3/2017 22:21	61	15/3/2017 19:26	61	17/3/2017 20:31	61	19/3/2017 9:36	61
11/3/2017 20:16	60	12/3/2017 13:21	61	12/3/2017 22:26	60	15/3/2017 19:31	62	17/3/2017 20:36	62	19/3/2017 9:41	61
11/3/2017 20:21	60	12/3/2017 13:26	60	12/3/2017 22:31	59	15/3/2017 19:36	62	17/3/2017 20:41	62	19/3/2017 9:46	61
11/3/2017 20:26	60	12/3/2017 13:31	61	12/3/2017 22:36	60	15/3/2017 19:41	61	17/3/2017 20:46	61	19/3/2017 9:51	62
11/3/2017 20:31	62	12/3/2017 13:36	61	12/3/2017 22:41	59	15/3/2017 19:46	63	17/3/2017 20:51	60	19/3/2017 9:56	61
11/3/2017 20:36	63	12/3/2017 13:41	59	12/3/2017 22:46	58	15/3/2017 19:51	62	17/3/2017 20:56	61	19/3/2017 10:01	61
11/3/2017 20:41	59	12/3/2017 13:46	63	12/3/2017 22:51	59	15/3/2017 19:56	61	17/3/2017 21:01	61	19/3/2017 10:06	60
11/3/2017 20:46	60	12/3/2017 13:51	62	12/3/2017 22:56	59	15/3/2017 20:01	61	17/3/2017 21:06	60	19/3/2017 10:11	60
11/3/2017 20:51	61	12/3/2017 13:56	62	13/3/2017 19:01	62	15/3/2017 20:06	62	17/3/2017 21:11	60	19/3/2017 10:16	61
11/3/2017 20:56	60	12/3/2017 14:01	59	13/3/2017 19:06	61	15/3/2017 20:11	62	17/3/2017 21:16	60	19/3/2017 10:21	62
11/3/2017 21:01	60	12/3/2017 14:06	60	13/3/2017 19:11	60	15/3/2017 20:16	62	17/3/2017 21:21	60	19/3/2017 10:26	61
11/3/2017 21:06	60	12/3/2017 14:11	60	13/3/2017 19:16	61	15/3/2017 20:21	60	17/3/2017 21:26	61	19/3/2017 10:31	61
11/3/2017 21:11	60	12/3/2017 14:16	61	13/3/2017 19:21	62	15/3/2017 20:26	62	17/3/2017 21:31	60	19/3/2017 10:36	60
11/3/2017 21:16	62	12/3/2017 14:21	62	13/3/2017 19:26	62	15/3/2017 20:31	61	17/3/2017 21:36	60	19/3/2017 10:41	61
11/3/2017 21:21	61	12/3/2017 14:26	62	13/3/2017 19:31	61	15/3/2017 20:36	61	17/3/2017 21:41	61	19/3/2017 10:46	60
11/3/2017 21:26	60	12/3/2017 14:31	63	13/3/2017 19:36	62	15/3/2017 20:41	60	17/3/2017 21:46	60	19/3/2017 10:51	60
11/3/2017 21:31	60	12/3/2017 14:36	59	13/3/2017 19:41	61	15/3/2017 20:46	61	17/3/2017 21:51	62	19/3/2017 10:56	60
11/3/2017 21:36	59	12/3/2017 14:41	60	13/3/2017 19:46	62	15/3/2017 20:51	60	17/3/2017 21:56	61	19/3/2017 11:01	60
11/3/2017 21:41	60	12/3/2017 14:46	59	13/3/2017 19:51	63	15/3/2017 20:56	60	17/3/2017 22:01	60	19/3/2017 11:06	61
11/3/2017 21:46	60	12/3/2017 14:51	59	13/3/2017 19:56	60	15/3/2017 21:01	61	17/3/2017 22:06	61	19/3/2017 11:11	61
11/3/2017 21:51	61	12/3/2017 14:56	61	13/3/2017 20:01	61	15/3/2017 21:06	60	17/3/2017 22:11	60	19/3/2017 11:16	59
11/3/2017 21:56	60	12/3/2017 15:01	59	13/3/2017 20:06	61	15/3/2017 21:11	60	17/3/2017 22:16	61	19/3/2017 11:21	60
11/3/2017 22:01	61	12/3/2017 15:06	59	13/3/2017 20:11	60	15/3/2017 21:16	60	17/3/2017 22:21	61	19/3/2017 11:26	59
11/3/2017 22:06	60	12/3/2017 15:11	60	13/3/2017 20:16	62	15/3/2017 21:21	60	17/3/2017 22:26	61	19/3/2017 11:31	60
11/3/2017 22:11	60	12/3/2017 15:16	59	13/3/2017 20:21	60	15/3/2017 21:26	60	17/3/2017 22:31	60	19/3/2017 11:36	61
11/3/2017 22:16	61	12/3/2017 15:21	60	13/3/2017 20:26	60	15/3/2017 21:31	60	17/3/2017 22:36	62	19/3/2017 11:41	61
11/3/2017 22:21	59	12/3/2017 15:26	62	13/3/2017 20:31	61	15/3/2017 21:36	60	17/3/2017 22:41	60	19/3/2017 11:46	61
11/3/2017 22:26	60	12/3/2017 15:31	61	13/3/2017 20:36	60	15/3/2017 21:41	60	17/3/2017 22:46	60	19/3/2017 11:51	62
11/3/2017 22:31	60	12/3/2017 15:36	59	13/3/2017 20:41	61	15/3/2017 21:46	60	17/3/2017 22:51	60	19/3/2017 11:56	63
11/3/2017 22:36	59	12/3/2017 15:41	56	13/3/2017 20:46	60	15/3/2017 21:51	62	17/3/2017 22:56	60	19/3/2017 12:01	62
11/3/2017 22:41	60	12/3/2017 15:46	61	13/3/2017 20:51	61	15/3/2017 21:56	60	18/3/2017 19:01	60	19/3/2017 12:06	63
11/3/2017 22:46	60	12/3/2017 15:51	61	13/3/2017 20:56	60	15/3/2017 22:01	60	18/3/2017 19:06	59	19/3/2017 12:11	63
11/3/2017 22:51	59	12/3/2017 15:56	63	13/3/2017 21:01	60	15/3/2017 22:06	60	18/3/2017 19:11	59	19/3/2017 12:16	63
11/3/2017 22:56	60	12/3/2017 16:01	61	13/3/2017 21:06	60	15/3/2017 22:11	60	18/3/2017 19:16	60	19/3/2017 12:21	63
12/3/2017 7:01	59	12/3/2017 16:06	60	13/3/2017 21:11	60	15/3/2017 22:16	60	18/3/2017 19:21	60	19/3/2017 12:26	63
12/3/2017 7:06	61	12/3/2017 16:11	60	13/3/2017 21:16	60	15/3/2017 22:21	62	18/3/2017 19:26	61	19/3/2017 12:31	55
12/3/2017 7:11	60	12/3/2017 16:16	60	13/3/2017 21:21	60	15/3/2017 22:26	61	18/3/2017 19:31	61	19/3/2017 12:36	62
12/3/2017 7:16	58	12/3/2017 16:21	60	13/3/2017 21:26	60	15/3/2017 22:31	61	18/3/2017 19:36	61	19/3/2017 12:41	64
12/3/2017 7:21	60	12/3/2017 16:26	61	13/3/2017 21:31	60	15/3/2017 22:36	61	18/3/2017 19:41	61	19/3/2017 12:46	63
12/3/2017 7:26	60	12/3/2017 16:31	62	13/3/2017 21:36	60	15/3/2017 22:41	60	18/3/2017 19:46	61	19/3/2017 12:51	62
12/3/2017 7:31	59	12/3/2017 16:36	60	13/3/2017 21:41	60	15/3/2017 22:46	59	18/3/2017 19:51	60	19/3/2017 12:56	62
12/3/2017 7:36	59	12/3/2017 16:41	59	13/3/2017 21:46	60	15/3/2017 22:51	59	18/3/2017 19:56	62	19/3/2017 13:01	62
12/3/2017 7:41	60	12/3/2017 16:46	60	13/3/2017 21:51	60	15/3/2017 22:56	60	18/3/2017 20:01	60	19/3/2017 13:06	62
12/3/2017 7:46	59	12/3/2017 16:51	60	13/3/2017 21:56	60	16/3/2017 19:01	62	18/3/2017 20:06	61	19/3/2017 13:11	52
12/3/2017 7:51	60	12/3/2017 16:56	60	13/3/2017 22:01	60	16/3/2017 19:06	62	18/3/2017 20:11	61	19/3/2017 13:16	64
12/3/2017 7:56	60	12/3/2017 17:01	60	13/3/2017 22:06	59	16/3/2017 19:11	62	18/3/2017 20:16	60	19/3/2017 13:21	51
12/3/2017 8:01	60	12/3/2017 17:06	59	13/3/2017 22:11	60	16/3/2017 19:16	62	18/3/2017 20:21	60	19/3/2017 13:26	62
12/3/2017 8:06	60	12/3/2017 17:11	60	13/3/2017 22:16	60	16/3/2017 19:21	62	18/3/2017 20:26	61	19/3/2017 13:31	62
12/3/2017 8:11	61	12/3/2017 17:16	59	13/3/2017 22:21	60	16/3/2017 19:26	61	18/3/2017 20:31	59	19/3/2017 13:36	62
12/3/2017 8:16	60	12/3/2017 17:21	60	13/3/2017 22:26	59	16/3/2017 19:31	62	18/3/2017 20:36	60	19/3/2017 13:41	61
12/3/2017 8:21	60	12/3/2017 17:26	53	13/3/2017 22:31	61	16/3/2017 19:36	62	18/3/2017 20:41	62	19/3/2017 13:46	62
12/3/2017 8:26	61	12/3/2017 17:31	61	13/3/2017 22:36	61	16/3/2017 19:41	63	18/3/2017 20:46	60	19/3/2017 13:51	62
12/3/2017 8:31	60	12/3/2017 17:36	61	13/3/2017 22:41	59	16/3/2017 19:46	61	18/3/2017 20:51	60	19/3/2017 13:56	63
12/3/2017 8:36	61	12/3/2017 17:41	63	13/3/2017 22:46	60	16/3/2017 19:51	63	18/3/2017 20:56	60	19/3/2017 14:01	63
12/3/2017 8:41	60	12/3/2017 17:46	61	13/3/2017 22:51	59	16/3/2017 19:56	62	18/3/2017 21:01	60	19/3/2017 14:06	63
12/3/2017 8:46	60	12/3/2017 17:51	60	13/3/2017 22:56	60	16/3/2017 20:01	62	18/3/2017 21:06	61	19/3/2017 14:11	62
12/3/2017 8:51	61	12/3/2017 17:56	60	14/3/2017 19:01	61	16/3/2017 20:06	61	18/3/2017 21:11	60	19/3/2017 14:16	57
12/3/2017 8:56	61	12/3/2017 18:01	60	14/3/2017 19:06	61	16/3/2017 20:11	62	18/3/2017 21:16	61	19/3/2017 14:21	62
12/3/2017 9:01	61	12/3/2017 18:06	59	14/3/2017 19:11	61	16/3/2017 20:16	63	18/3/2017 21:21	61	19/3/2017 14:26	61
12/3/2017 9:06	62	12/3/2017 18:11	59	14/3/2017 19:16	61	16/3/2017 20:21	61	18/3/2017 21:26	60	19/3/2017 14:31	62
12/3/2017 9:11	61	12/3/2017 18:16	56	14/3/2017 19:21	60	16/3/2017 20:26	61	18/3/2017 21:31	60	19/3/2017 14:36	61
12/3/2017 9:16	61	12/3/2017 18:21	62	14/3/2017 19:26	60	16/3/2017 20:31	62	18/3/2017 21:36	61	19/3/2017 14:41	61
12/3/2017 9:21	61	12/3/2017 18:26	61	14/3/2017 19:31	62	16/3/2017 20:36	63	18/3/2017 21:41	60	19/3/2017 14:46	61
12/3/2017 9:26	61	12/3/2017 18:31	62	14/3/2017 19:36	62	16/3/2017 20:41	61	18/3/2017 21:46	61	19/3/2017 14:51	62
12/3/2017 9:31	61	12/3/2017 18:36	60	14/3/2017 19:41	61	16/3/2017 20:46	60	18/3/2017 21:51	60	19/3/2017 14:56	61
12/3/2017 9:36	60	12/3/2017 18:41	58	14/3/2017 19:46	61						

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
19/3/2017 18:01	61	21/3/2017 19:06	61	23/3/2017 20:11	62	25/3/2017 21:16	61	26/3/2017 14:21	61	Night time: 23:00-07:00	
19/3/2017 18:06	62	21/3/2017 19:11	60	23/3/2017 20:16	61	25/3/2017 21:21	61	26/3/2017 14:26	60		
19/3/2017 18:11	61	21/3/2017 19:16	60	23/3/2017 20:21	61	25/3/2017 21:26	61	26/3/2017 14:31	61	27/2/2017 0:01	58
19/3/2017 18:16	60	21/3/2017 19:21	61	23/3/2017 20:26	62	25/3/2017 21:31	60	26/3/2017 14:36	61	27/2/2017 0:06	58
19/3/2017 18:21	62	21/3/2017 19:26	61	23/3/2017 20:31	61	25/3/2017 21:36	60	26/3/2017 14:41	60	27/2/2017 0:11	58
19/3/2017 18:26	62	21/3/2017 19:31	62	23/3/2017 20:36	62	25/3/2017 21:41	60	26/3/2017 14:46	60	27/2/2017 0:16	58
19/3/2017 18:31	61	21/3/2017 19:36	61	23/3/2017 20:41	61	25/3/2017 21:46	60	26/3/2017 14:51	61	27/2/2017 0:21	57
19/3/2017 18:36	61	21/3/2017 19:41	61	23/3/2017 20:46	61	25/3/2017 21:51	61	26/3/2017 14:56	61	27/2/2017 0:26	57
19/3/2017 18:41	61	21/3/2017 19:46	61	23/3/2017 20:51	60	25/3/2017 21:56	60	26/3/2017 15:01	60	27/2/2017 0:31	57
19/3/2017 18:46	61	21/3/2017 19:51	60	23/3/2017 20:56	61	25/3/2017 22:01	61	26/3/2017 15:06	61	27/2/2017 0:36	58
19/3/2017 18:51	61	21/3/2017 19:56	61	23/3/2017 21:01	60	25/3/2017 22:06	60	26/3/2017 15:11	63	27/2/2017 0:41	57
19/3/2017 18:56	61	21/3/2017 20:01	61	23/3/2017 21:06	63	25/3/2017 22:11	60	26/3/2017 15:16	61	27/2/2017 0:46	57
19/3/2017 19:01	61	21/3/2017 20:06	61	23/3/2017 21:11	61	25/3/2017 22:16	60	26/3/2017 15:21	61	27/2/2017 0:51	56
19/3/2017 19:06	61	21/3/2017 20:11	62	23/3/2017 21:16	64	25/3/2017 22:21	60	26/3/2017 15:26	61	27/2/2017 0:56	56
19/3/2017 19:11	61	21/3/2017 20:16	61	23/3/2017 21:21	60	25/3/2017 22:26	61	26/3/2017 15:31	60	27/2/2017 1:01	57
19/3/2017 19:16	61	21/3/2017 20:21	61	23/3/2017 21:26	62	25/3/2017 22:31	60	26/3/2017 15:36	62	27/2/2017 1:06	57
19/3/2017 19:21	61	21/3/2017 20:26	61	23/3/2017 21:31	60	25/3/2017 22:36	61	26/3/2017 15:41	61	27/2/2017 1:11	56
19/3/2017 19:26	61	21/3/2017 20:31	60	23/3/2017 21:36	61	25/3/2017 22:41	62	26/3/2017 15:46	62	27/2/2017 1:16	57
19/3/2017 19:31	61	21/3/2017 20:36	61	23/3/2017 21:41	60	25/3/2017 22:46	61	26/3/2017 15:51	61	27/2/2017 1:21	56
19/3/2017 19:36	61	21/3/2017 20:41	60	23/3/2017 21:46	61	25/3/2017 22:51	59	26/3/2017 15:56	61	27/2/2017 1:26	56
19/3/2017 19:41	61	21/3/2017 20:46	60	23/3/2017 21:51	60	25/3/2017 22:56	59	26/3/2017 16:01	63	27/2/2017 1:31	56
19/3/2017 19:46	61	21/3/2017 20:51	61	23/3/2017 21:56	60	26/3/2017 7:01	59	26/3/2017 16:06	61	27/2/2017 1:36	55
19/3/2017 19:51	60	21/3/2017 20:56	61	23/3/2017 22:01	59	26/3/2017 7:06	60	26/3/2017 16:11	62	27/2/2017 1:41	55
19/3/2017 19:56	60	21/3/2017 21:01	60	23/3/2017 22:06	61	26/3/2017 7:11	59	26/3/2017 16:16	61	27/2/2017 1:46	56
19/3/2017 20:01	60	21/3/2017 21:06	59	23/3/2017 22:11	62	26/3/2017 7:16	59	26/3/2017 16:21	61	27/2/2017 1:51	56
19/3/2017 20:06	60	21/3/2017 21:11	60	23/3/2017 22:16	60	26/3/2017 7:21	59	26/3/2017 16:26	61	27/2/2017 1:56	57
19/3/2017 20:11	61	21/3/2017 21:16	60	23/3/2017 22:21	60	26/3/2017 7:26	59	26/3/2017 16:31	63	27/2/2017 2:01	54
19/3/2017 20:16	60	21/3/2017 21:21	60	23/3/2017 22:26	61	26/3/2017 7:31	60	26/3/2017 16:36	61	27/2/2017 2:06	56
19/3/2017 20:21	61	21/3/2017 21:26	60	23/3/2017 22:31	61	26/3/2017 7:36	59	26/3/2017 16:41	61	27/2/2017 2:11	56
19/3/2017 20:26	61	21/3/2017 21:31	60	23/3/2017 22:36	60	26/3/2017 7:41	60	26/3/2017 16:46	62	27/2/2017 2:16	54
19/3/2017 20:31	61	21/3/2017 21:36	60	23/3/2017 22:41	60	26/3/2017 7:46	59	26/3/2017 16:51	62	27/2/2017 2:21	55
19/3/2017 20:36	60	21/3/2017 21:41	60	23/3/2017 22:46	60	26/3/2017 7:51	59	26/3/2017 16:56	61	27/2/2017 2:26	55
19/3/2017 20:41	59	21/3/2017 21:46	60	23/3/2017 22:51	61	26/3/2017 7:56	60	26/3/2017 17:01	61	27/2/2017 2:31	56
19/3/2017 20:46	60	21/3/2017 21:51	59	23/3/2017 22:56	60	26/3/2017 8:01	60	26/3/2017 17:06	62	27/2/2017 2:36	55
19/3/2017 20:51	60	21/3/2017 21:56	58	24/3/2017 19:01	59	26/3/2017 8:06	61	26/3/2017 17:11	61	27/2/2017 2:41	55
19/3/2017 20:56	60	21/3/2017 22:01	59	24/3/2017 19:06	60	26/3/2017 8:11	60	26/3/2017 17:16	61	27/2/2017 2:46	55
19/3/2017 21:01	60	21/3/2017 22:06	59	24/3/2017 19:11	61	26/3/2017 8:16	60	26/3/2017 17:21	60	27/2/2017 2:51	54
19/3/2017 21:06	60	21/3/2017 22:11	59	24/3/2017 19:16	60	26/3/2017 8:21	60	26/3/2017 17:26	61	27/2/2017 2:56	57
19/3/2017 21:11	60	21/3/2017 22:16	59	24/3/2017 19:21	61	26/3/2017 8:26	60	26/3/2017 17:31	61	27/2/2017 3:01	53
19/3/2017 21:16	59	21/3/2017 22:21	61	24/3/2017 19:26	61	26/3/2017 8:31	61	26/3/2017 17:36	62	27/2/2017 3:06	54
19/3/2017 21:21	60	21/3/2017 22:26	59	24/3/2017 19:31	61	26/3/2017 8:36	61	26/3/2017 17:41	61	27/2/2017 3:11	54
19/3/2017 21:26	60	21/3/2017 22:31	59	24/3/2017 19:36	62	26/3/2017 8:41	60	26/3/2017 17:46	60	27/2/2017 3:16	54
19/3/2017 21:31	60	21/3/2017 22:36	59	24/3/2017 19:41	62	26/3/2017 8:46	61	26/3/2017 17:51	60	27/2/2017 3:21	55
19/3/2017 21:36	61	21/3/2017 22:41	59	24/3/2017 19:46	63	26/3/2017 8:51	61	26/3/2017 17:56	61	27/2/2017 3:26	55
19/3/2017 21:41	59	21/3/2017 22:46	58	24/3/2017 19:51	61	26/3/2017 8:56	61	26/3/2017 18:01	62	27/2/2017 3:31	55
19/3/2017 21:46	60	21/3/2017 22:51	59	24/3/2017 19:56	63	26/3/2017 9:01	62	26/3/2017 18:06	60	27/2/2017 3:36	54
19/3/2017 21:51	60	21/3/2017 22:56	59	24/3/2017 20:01	62	26/3/2017 9:06	61	26/3/2017 18:11	61	27/2/2017 3:41	54
19/3/2017 21:56	60	22/3/2017 19:01	63	24/3/2017 20:06	61	26/3/2017 9:11	61	26/3/2017 18:16	61	27/2/2017 3:46	55
19/3/2017 22:01	59	22/3/2017 19:06	62	24/3/2017 20:11	61	26/3/2017 9:16	61	26/3/2017 18:21	61	27/2/2017 3:51	55
19/3/2017 22:06	60	22/3/2017 19:11	61	24/3/2017 20:16	61	26/3/2017 9:21	61	26/3/2017 18:26	61	27/2/2017 3:56	54
19/3/2017 22:11	59	22/3/2017 19:16	62	24/3/2017 20:21	61	26/3/2017 9:26	62	26/3/2017 18:31	59	27/2/2017 4:01	55
19/3/2017 22:16	60	22/3/2017 19:21	62	24/3/2017 20:26	61	26/3/2017 9:31	61	26/3/2017 18:36	61	27/2/2017 4:06	54
19/3/2017 22:21	60	22/3/2017 19:26	62	24/3/2017 20:31	61	26/3/2017 9:36	61	26/3/2017 18:41	61	27/2/2017 4:11	53
19/3/2017 22:26	60	22/3/2017 19:31	62	24/3/2017 20:36	62	26/3/2017 9:41	61	26/3/2017 18:46	62	27/2/2017 4:16	54
19/3/2017 22:31	59	22/3/2017 19:36	62	24/3/2017 20:41	61	26/3/2017 9:46	62	26/3/2017 18:51	61	27/2/2017 4:21	54
19/3/2017 22:36	59	22/3/2017 19:41	62	24/3/2017 20:46	60	26/3/2017 9:51	62	26/3/2017 18:56	61	27/2/2017 4:26	55
19/3/2017 22:41	60	22/3/2017 19:46	61	24/3/2017 20:51	60	26/3/2017 9:56	62	26/3/2017 19:01	60	27/2/2017 4:31	54
19/3/2017 22:46	59	22/3/2017 19:51	61	24/3/2017 20:56	61	26/3/2017 10:01	63	26/3/2017 19:06	60	27/2/2017 4:36	54
19/3/2017 22:51	59	22/3/2017 19:56	62	24/3/2017 21:01	61	26/3/2017 10:06	62	26/3/2017 19:11	61	27/2/2017 4:41	54
19/3/2017 22:56	59	22/3/2017 20:01	62	24/3/2017 21:06	63	26/3/2017 10:11	62	26/3/2017 19:16	61	27/2/2017 4:46	55
20/3/2017 19:01	60	22/3/2017 20:06	61	24/3/2017 21:11	60	26/3/2017 10:16	62	26/3/2017 19:21	61	27/2/2017 4:51	54
20/3/2017 19:06	59	22/3/2017 20:11	63	24/3/2017 21:16	60	26/3/2017 10:21	60	26/3/2017 19:26	61	27/2/2017 4:56	55
20/3/2017 19:11	59	22/3/2017 20:16	62	24/3/2017 21:21	60	26/3/2017 10:26	61	26/3/2017 19:31	61	27/2/2017 5:01	55
20/3/2017 19:16	60	22/3/2017 20:21	62	24/3/2017 21:26	59	26/3/2017 10:31	60	26/3/2017 19:36	61	27/2/2017 5:06	55
20/3/2017 19:21	60	22/3/2017 20:26	61	24/3/2017 21:31	60	26/3/2017 10:36	60	26/3/2017 19:41	60	27/2/2017 5:11	55
20/3/2017 19:26	59	22/3/2017 20:31	62	24/3/2017 21:36	60	26/3/2017 10:41	60	26/3/2017 19:46	60	27/2/2017 5:16	55
20/3/2017 19:31	61	22/3/2017 20:36	61	24/3/2017 21:41	61	26/3/2017 10:46	61	26/3/2017 19:51	60	27/2/2017 5:21	56
20/3/2017 19:36	60	22/3/2017 20:41	61	24/3/2017 21:46	53	26/3/2017 10:51	59	26/3/2017 19:56	59	27/2/2017 5:26	56
20/3/2017 19:41	61	22/3/2017 20:46	61	24/3/2017 21:51	61	26/3/2017 10:56	62	26/3/2017 20:01	59	27/2/2017 5:31	56
20/3/2017 19:46	61	22/3/2017 20:51	61	24/3/2017 21:56	60	26/3/2017 11:01	62	26/3/2017 20:06	60	27/2/2017 5:36	56
20/3/2017 19:51	61	22/3/2017 20:56	61	24/3/2017 22:01	60	26/3/2017 11:06	60	26/3/2017 20:11	60	27/2/2017 5:41	56
20/3/2017 19:56	61	22/3/2017 21:01	61	24/3/2017 22:06	63	26/3/2017 11:11	59	26/3/2017 20:16	60	27/2/2017 5:46	56
20/3/2017 20:01	61	22/3/2017 21:06	61	24/3/2017 22:11	61	26/3/2017 11:16	60	26/3/2017 20:21	60	27/2/2017 5:51	58
20/3/2017 20:06	63	22/3/2017 21:11	61								

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
28/2/2017 0:56	56	1/3/2017 2:01	56	2/3/2017 3:06	54	3/3/2017 4:11	60	4/3/2017 5:16	55	5/3/2017 6:21	58
28/2/2017 1:01	60	1/3/2017 2:06	56	2/3/2017 3:11	56	3/3/2017 4:16	60	4/3/2017 5:21	56	5/3/2017 6:26	59
28/2/2017 1:06	57	1/3/2017 2:11	55	2/3/2017 3:16	55	3/3/2017 4:21	61	4/3/2017 5:26	58	5/3/2017 6:31	59
28/2/2017 1:11	56	1/3/2017 2:16	56	2/3/2017 3:21	54	3/3/2017 4:26	60	4/3/2017 5:31	56	5/3/2017 6:36	58
28/2/2017 1:16	56	1/3/2017 2:21	56	2/3/2017 3:26	54	3/3/2017 4:31	60	4/3/2017 5:36	56	5/3/2017 6:41	59
28/2/2017 1:21	57	1/3/2017 2:26	56	2/3/2017 3:31	55	3/3/2017 4:36	60	4/3/2017 5:41	57	5/3/2017 6:46	59
28/2/2017 1:26	56	1/3/2017 2:31	55	2/3/2017 3:36	55	3/3/2017 4:41	60	4/3/2017 5:46	56	5/3/2017 6:51	59
28/2/2017 1:31	56	1/3/2017 2:36	55	2/3/2017 3:41	54	3/3/2017 4:46	60	4/3/2017 5:51	57	5/3/2017 6:56	59
28/2/2017 1:36	56	1/3/2017 2:41	55	2/3/2017 3:46	55	3/3/2017 4:51	60	4/3/2017 5:56	57	5/3/2017 7:01	59
28/2/2017 1:41	56	1/3/2017 2:46	55	2/3/2017 3:51	55	3/3/2017 4:56	61	4/3/2017 6:01	56	5/3/2017 7:06	58
28/2/2017 1:46	57	1/3/2017 2:51	54	2/3/2017 3:56	54	3/3/2017 5:01	60	4/3/2017 6:06	57	5/3/2017 7:11	59
28/2/2017 1:51	55	1/3/2017 2:56	55	2/3/2017 4:01	54	3/3/2017 5:06	61	4/3/2017 6:11	57	5/3/2017 7:16	58
28/2/2017 1:56	55	1/3/2017 3:01	55	2/3/2017 4:06	54	3/3/2017 5:11	60	4/3/2017 6:16	59	5/3/2017 7:21	58
28/2/2017 2:01	56	1/3/2017 3:06	54	2/3/2017 4:11	55	3/3/2017 5:16	60	4/3/2017 6:21	58	5/3/2017 7:26	58
28/2/2017 2:06	55	1/3/2017 3:11	55	2/3/2017 4:16	55	3/3/2017 5:21	61	4/3/2017 6:26	58	5/3/2017 7:31	57
28/2/2017 2:11	55	1/3/2017 3:16	54	2/3/2017 4:21	54	3/3/2017 5:26	60	4/3/2017 6:31	58	5/3/2017 7:36	57
28/2/2017 2:16	55	1/3/2017 3:21	54	2/3/2017 4:26	55	3/3/2017 5:31	61	4/3/2017 6:36	60	5/3/2017 7:41	58
28/2/2017 2:21	56	1/3/2017 3:26	54	2/3/2017 4:31	56	3/3/2017 5:36	61	4/3/2017 6:41	59	5/3/2017 7:46	57
28/2/2017 2:26	55	1/3/2017 3:31	55	2/3/2017 4:36	54	3/3/2017 5:41	60	4/3/2017 6:46	60	5/3/2017 7:51	57
28/2/2017 2:31	55	1/3/2017 3:36	56	2/3/2017 4:41	56	3/3/2017 5:46	44	4/3/2017 6:51	61	5/3/2017 7:56	57
28/2/2017 2:36	56	1/3/2017 3:41	55	2/3/2017 4:46	55	3/3/2017 5:51	61	4/3/2017 6:56	59	6/3/2017 0:01	57
28/2/2017 2:41	55	1/3/2017 3:46	55	2/3/2017 4:51	56	3/3/2017 5:56	60	4/3/2017 7:01	59	6/3/2017 0:06	58
28/2/2017 2:46	55	1/3/2017 3:51	55	2/3/2017 4:56	55	3/3/2017 6:01	60	4/3/2017 7:06	59	6/3/2017 0:11	57
28/2/2017 2:51	54	1/3/2017 3:56	54	2/3/2017 5:01	55	3/3/2017 6:06	61	4/3/2017 7:11	60	6/3/2017 0:16	57
28/2/2017 2:56	55	1/3/2017 4:01	54	2/3/2017 5:06	54	3/3/2017 6:11	60	4/3/2017 7:16	59	6/3/2017 0:21	56
28/2/2017 3:01	55	1/3/2017 4:06	54	2/3/2017 5:11	55	3/3/2017 6:16	61	4/3/2017 7:21	59	6/3/2017 0:26	56
28/2/2017 3:06	55	1/3/2017 4:11	55	2/3/2017 5:16	55	3/3/2017 6:21	51	4/3/2017 7:26	59	6/3/2017 0:31	57
28/2/2017 3:11	55	1/3/2017 4:16	55	2/3/2017 5:21	56	3/3/2017 6:26	55	4/3/2017 7:31	59	6/3/2017 0:36	56
28/2/2017 3:16	55	1/3/2017 4:21	55	2/3/2017 5:26	56	3/3/2017 6:31	53	4/3/2017 7:36	59	6/3/2017 0:41	56
28/2/2017 3:21	57	1/3/2017 4:26	55	2/3/2017 5:31	55	3/3/2017 6:36	58	4/3/2017 7:41	60	6/3/2017 0:46	56
28/2/2017 3:26	53	1/3/2017 4:31	56	2/3/2017 5:36	56	3/3/2017 6:41	58	4/3/2017 7:46	58	6/3/2017 0:51	58
28/2/2017 3:31	55	1/3/2017 4:36	57	2/3/2017 5:41	56	3/3/2017 6:46	57	4/3/2017 7:51	58	6/3/2017 0:56	56
28/2/2017 3:36	55	1/3/2017 4:41	54	2/3/2017 5:46	57	3/3/2017 6:51	59	4/3/2017 7:56	58	6/3/2017 1:01	56
28/2/2017 3:41	55	1/3/2017 4:46	55	2/3/2017 5:51	57	3/3/2017 6:56	58	5/3/2017 0:01	58	6/3/2017 1:06	56
28/2/2017 3:46	55	1/3/2017 4:51	56	2/3/2017 5:56	57	3/3/2017 7:01	60	5/3/2017 0:06	59	6/3/2017 1:11	56
28/2/2017 3:51	55	1/3/2017 4:56	54	2/3/2017 6:01	57	3/3/2017 7:06	59	5/3/2017 0:11	58	6/3/2017 1:16	57
28/2/2017 3:56	54	1/3/2017 5:01	56	2/3/2017 6:06	57	3/3/2017 7:11	49	5/3/2017 0:16	58	6/3/2017 1:21	56
28/2/2017 4:01	55	1/3/2017 5:06	55	2/3/2017 6:11	58	3/3/2017 7:16	60	5/3/2017 0:21	58	6/3/2017 1:26	56
28/2/2017 4:06	55	1/3/2017 5:11	55	2/3/2017 6:16	59	3/3/2017 7:21	59	5/3/2017 0:26	59	6/3/2017 1:31	55
28/2/2017 4:11	54	1/3/2017 5:16	54	2/3/2017 6:21	59	3/3/2017 7:26	59	5/3/2017 0:31	58	6/3/2017 1:36	56
28/2/2017 4:16	54	1/3/2017 5:21	56	2/3/2017 6:26	60	3/3/2017 7:31	59	5/3/2017 0:36	57	6/3/2017 1:41	55
28/2/2017 4:21	55	1/3/2017 5:26	55	2/3/2017 6:31	59	3/3/2017 7:36	60	5/3/2017 0:41	58	6/3/2017 1:46	55
28/2/2017 4:26	55	1/3/2017 5:31	56	2/3/2017 6:36	60	3/3/2017 7:41	59	5/3/2017 0:46	58	6/3/2017 1:51	55
28/2/2017 4:31	55	1/3/2017 5:36	55	2/3/2017 6:41	60	3/3/2017 7:46	59	5/3/2017 0:51	57	6/3/2017 1:56	55
28/2/2017 4:36	55	1/3/2017 5:41	57	2/3/2017 6:46	60	3/3/2017 7:51	59	5/3/2017 0:56	58	6/3/2017 2:01	56
28/2/2017 4:41	54	1/3/2017 5:46	57	2/3/2017 6:51	61	3/3/2017 7:56	59	5/3/2017 1:01	57	6/3/2017 2:06	55
28/2/2017 4:46	56	1/3/2017 5:51	58	2/3/2017 6:56	60	4/3/2017 0:01	58	5/3/2017 1:06	58	6/3/2017 2:11	55
28/2/2017 4:51	54	1/3/2017 5:56	57	2/3/2017 7:01	52	4/3/2017 0:06	59	5/3/2017 1:11	57	6/3/2017 2:16	54
28/2/2017 4:56	55	1/3/2017 6:01	57	2/3/2017 7:06	61	4/3/2017 0:11	58	5/3/2017 1:16	57	6/3/2017 2:21	54
28/2/2017 5:01	54	1/3/2017 6:06	58	2/3/2017 7:11	57	4/3/2017 0:16	59	5/3/2017 1:21	57	6/3/2017 2:26	53
28/2/2017 5:06	54	1/3/2017 6:11	58	2/3/2017 7:16	46	4/3/2017 0:21	59	5/3/2017 1:26	58	6/3/2017 2:31	54
28/2/2017 5:11	55	1/3/2017 6:16	59	2/3/2017 7:21	61	4/3/2017 0:26	59	5/3/2017 1:31	57	6/3/2017 2:36	53
28/2/2017 5:16	56	1/3/2017 6:21	58	2/3/2017 7:26	61	4/3/2017 0:31	59	5/3/2017 1:36	58	6/3/2017 2:41	54
28/2/2017 5:21	56	1/3/2017 6:26	60	2/3/2017 7:31	60	4/3/2017 0:36	57	5/3/2017 1:41	57	6/3/2017 2:46	54
28/2/2017 5:26	56	1/3/2017 6:31	59	2/3/2017 7:36	60	4/3/2017 0:41	58	5/3/2017 1:46	56	6/3/2017 2:51	53
28/2/2017 5:31	56	1/3/2017 6:36	60	2/3/2017 7:41	61	4/3/2017 0:46	58	5/3/2017 1:51	56	6/3/2017 2:56	55
28/2/2017 5:36	56	1/3/2017 6:41	61	2/3/2017 7:46	60	4/3/2017 0:51	61	5/3/2017 1:56	56	6/3/2017 3:01	55
28/2/2017 5:41	56	1/3/2017 6:46	61	2/3/2017 7:51	60	4/3/2017 0:56	58	5/3/2017 2:01	57	6/3/2017 3:06	53
28/2/2017 5:46	56	1/3/2017 6:51	60	2/3/2017 7:56	60	4/3/2017 1:01	58	5/3/2017 2:06	55	6/3/2017 3:11	55
28/2/2017 5:51	58	1/3/2017 6:56	60	3/3/2017 0:01	46	4/3/2017 1:06	58	5/3/2017 2:11	56	6/3/2017 3:16	55
28/2/2017 5:56	56	1/3/2017 7:01	59	3/3/2017 0:06	61	4/3/2017 1:11	59	5/3/2017 2:16	57	6/3/2017 3:21	54
28/2/2017 6:01	57	1/3/2017 7:06	59	3/3/2017 0:11	46	4/3/2017 1:16	57	5/3/2017 2:21	58	6/3/2017 3:26	55
28/2/2017 6:06	58	1/3/2017 7:11	59	3/3/2017 0:16	49	4/3/2017 1:21	57	5/3/2017 2:26	56	6/3/2017 3:31	55
28/2/2017 6:11	57	1/3/2017 7:16	59	3/3/2017 0:21	54	4/3/2017 1:26	58	5/3/2017 2:31	56	6/3/2017 3:36	56
28/2/2017 6:16	59	1/3/2017 7:21	59	3/3/2017 0:26	52	4/3/2017 1:31	57	5/3/2017 2:36	57	6/3/2017 3:41	54
28/2/2017 6:21	58	1/3/2017 7:26	58	3/3/2017 0:31	51	4/3/2017 1:36	58	5/3/2017 2:41	56	6/3/2017 3:46	53
28/2/2017 6:26	60	1/3/2017 7:31	58	3/3/2017 0:36	51	4/3/2017 1:41	59	5/3/2017 2:46	56	6/3/2017 3:51	55
28/2/2017 6:31	60	1/3/2017 7:36	59	3/3/2017 0:41	52	4/3/2017 1:46	60	5/3/2017 2:51	55	6/3/2017 3:56	53
28/2/2017 6:36	60	1/3/2017 7:41	58	3/3/2017 0:46	61	4/3/2017 1:51	57	5/3/2017 2:56	55	6/3/2017 4:01	54
28/2/2017 6:41	61	1/3/2017 7:46	59	3/3/2017 0:51	61	4/3/2017 1:56	57	5/3/2017 3:01	56	6/3/2017 4:06	53
28/2/2017 6:46	61	1/3/2017 7:51	58	3/3/2017 0:56	61	4/3/2017 2:01	57	5/3/2017 3:06	56	6/3/2017 4:11	55
28/2/2017 6:51	38	1/3/2017 7:56	58	3/3/2017 1:01	60	4/3/2017 2:06	57	5/3/2017 3:11	55	6/3/2017 4:16	55
28/2/2017 6:56	60	2/3/2017 0:01	58	3/3/2017 1:06	60	4/3/2017 2:11	57	5/3/2017 3:16	55	6/3/2017 4:21	54
28/2/2017 7:01	59	2/3/2017 0:06	58	3/3/2017 1:11	60	4/3/2017 2:16	56	5/3/2017 3:21	55	6/3/2017 4:26	55
28/2/2017 7:06	60	2/3/2017 0:11	57	3/3/2017 1:16	50	4/3/2017 2:21	56	5/3/2017 3:26	56	6/3/2017 4:31	54
28/2/2017 7:11	59	2/3/2017 0:16	57	3/3/2017 1:21	48	4/3/2017 2:26	57	5/3/2017 3:31	55	6/3/2017 4:36	54
28/2/2017 7:16	60	2/3/2017 0:21	58	3/3/2017 1:26	52	4/3/2017 2:31	56	5/3/2017 3:36	55	6/3/2017 4:41	54
28/2/2017 7:21	59	2/3/2017 0:26	58	3/3/2017 1:31	53	4/3/2017 2:36	56	5/3/2017 3:41	56	6/3/2017 4:46	55
28/2/2017 7:26	60	2/3/2017 0:31	58	3/3							

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)											
6/3/2017 23:26	59	8/3/2017 0:31	57	9/3/2017 1:36	59	10/3/2017 2:41	56	11/3/2017 3:46	56	12/3/2017 4:51	55		
6/3/2017 23:31	58	8/3/2017 0:36	57	9/3/2017 1:41	59	10/3/2017 2:46	56	11/3/2017 3:51	56	12/3/2017 4:56	56		
6/3/2017 23:36	58	8/3/2017 0:41	56	9/3/2017 1:46	59	10/3/2017 2:51	56	11/3/2017 3:56	56	12/3/2017 5:01	55		
6/3/2017 23:41	58	8/3/2017 0:46	57	9/3/2017 1:51	59	10/3/2017 2:56	57	11/3/2017 4:01	56	12/3/2017 5:06	55		
6/3/2017 23:46	58	8/3/2017 0:51	56	9/3/2017 1:56	59	10/3/2017 3:01	54	11/3/2017 4:06	56	12/3/2017 5:11	56		
6/3/2017 23:51	57	8/3/2017 0:56	58	9/3/2017 2:01	59	10/3/2017 3:06	55	11/3/2017 4:11	56	12/3/2017 5:16	55		
6/3/2017 23:56	58	8/3/2017 1:01	57	9/3/2017 2:06	59	10/3/2017 3:11	55	11/3/2017 4:16	56	12/3/2017 5:21	56		
7/3/2017 0:01	61	8/3/2017 1:06	57	9/3/2017 2:11	58	10/3/2017 3:16	54	11/3/2017 4:21	56	12/3/2017 5:26	56		
7/3/2017 0:06	59	8/3/2017 1:11	56	9/3/2017 2:16	58	10/3/2017 3:21	56	11/3/2017 4:26	56	12/3/2017 5:31	56		
7/3/2017 0:11	59	8/3/2017 1:16	57	9/3/2017 2:21	58	10/3/2017 3:26	55	11/3/2017 4:31	55	12/3/2017 5:36	57		
7/3/2017 0:16	57	8/3/2017 1:21	56	9/3/2017 2:26	60	10/3/2017 3:31	55	11/3/2017 4:36	56	12/3/2017 5:41	57		
7/3/2017 0:21	58	8/3/2017 1:26	56	9/3/2017 2:31	59	10/3/2017 3:36	55	11/3/2017 4:41	56	12/3/2017 5:46	58		
7/3/2017 0:26	57	8/3/2017 1:31	60	9/3/2017 2:36	58	10/3/2017 3:41	55	11/3/2017 4:46	55	12/3/2017 5:51	57		
7/3/2017 0:31	57	8/3/2017 1:36	56	9/3/2017 2:41	58	10/3/2017 3:46	56	11/3/2017 4:51	55	12/3/2017 5:56	57		
7/3/2017 0:36	58	8/3/2017 1:41	56	9/3/2017 2:46	58	10/3/2017 3:51	55	11/3/2017 4:56	56	12/3/2017 6:01	57		
7/3/2017 0:41	57	8/3/2017 1:46	56	9/3/2017 2:51	58	10/3/2017 3:56	56	11/3/2017 5:01	56	12/3/2017 6:06	57		
7/3/2017 0:46	57	8/3/2017 1:51	56	9/3/2017 2:56	58	10/3/2017 4:01	55	11/3/2017 5:06	56	12/3/2017 6:11	58		
7/3/2017 0:51	57	8/3/2017 1:56	55	9/3/2017 3:01	58	10/3/2017 4:06	55	11/3/2017 5:11	56	12/3/2017 6:16	57		
7/3/2017 0:56	58	8/3/2017 2:01	56	9/3/2017 3:06	58	10/3/2017 4:11	54	11/3/2017 5:16	54	12/3/2017 6:21	58		
7/3/2017 1:01	57	8/3/2017 2:06	55	9/3/2017 3:11	58	10/3/2017 4:16	55	11/3/2017 5:21	55	12/3/2017 6:26	59		
7/3/2017 1:06	57	8/3/2017 2:11	55	9/3/2017 3:16	58	10/3/2017 4:21	56	11/3/2017 5:26	56	12/3/2017 6:31	59		
7/3/2017 1:11	56	8/3/2017 2:16	55	9/3/2017 3:21	57	10/3/2017 4:26	55	11/3/2017 5:31	57	12/3/2017 6:36	59		
7/3/2017 1:16	57	8/3/2017 2:21	55	9/3/2017 3:26	58	10/3/2017 4:31	55	11/3/2017 5:36	56	12/3/2017 6:41	59		
7/3/2017 1:21	57	8/3/2017 2:26	55	9/3/2017 3:31	58	10/3/2017 4:36	54	11/3/2017 5:41	55	12/3/2017 6:46	60		
7/3/2017 1:26	56	8/3/2017 2:31	55	9/3/2017 3:36	58	10/3/2017 4:41	55	11/3/2017 5:46	57	12/3/2017 6:51	59		
7/3/2017 1:31	55	8/3/2017 2:36	56	9/3/2017 3:41	58	10/3/2017 4:46	55	11/3/2017 5:51	57	12/3/2017 6:56	59		
7/3/2017 1:36	57	8/3/2017 2:41	56	9/3/2017 3:46	57	10/3/2017 4:51	55	11/3/2017 5:56	56	12/3/2017 7:01	58		
7/3/2017 1:41	56	8/3/2017 2:46	56	9/3/2017 3:51	58	10/3/2017 4:56	55	11/3/2017 6:01	56	12/3/2017 7:06	59		
7/3/2017 1:46	55	8/3/2017 2:51	55	9/3/2017 3:56	58	10/3/2017 5:01	54	11/3/2017 6:06	57	12/3/2017 7:11	59		
7/3/2017 1:51	55	8/3/2017 2:56	54	9/3/2017 4:01	58	10/3/2017 5:06	55	11/3/2017 6:11	57	12/3/2017 7:16	58		
7/3/2017 1:56	55	8/3/2017 3:01	55	9/3/2017 4:06	57	10/3/2017 5:11	54	11/3/2017 6:16	57	12/3/2017 7:21	58		
7/3/2017 2:01	56	8/3/2017 3:06	54	9/3/2017 4:11	57	10/3/2017 5:16	55	11/3/2017 6:21	58	12/3/2017 7:26	58		
7/3/2017 2:06	56	8/3/2017 3:11	54	9/3/2017 4:16	57	10/3/2017 5:21	55	11/3/2017 6:26	59	12/3/2017 7:31	58		
7/3/2017 2:11	55	8/3/2017 3:16	54	9/3/2017 4:21	58	10/3/2017 5:26	56	11/3/2017 6:31	59	12/3/2017 7:36	58		
7/3/2017 2:16	54	8/3/2017 3:21	54	9/3/2017 4:26	58	10/3/2017 5:31	56	11/3/2017 6:36	59	12/3/2017 7:41	59		
7/3/2017 2:21	55	8/3/2017 3:26	54	9/3/2017 4:31	58	10/3/2017 5:36	56	11/3/2017 6:41	59	12/3/2017 7:46	58		
7/3/2017 2:26	55	8/3/2017 3:31	55	9/3/2017 4:36	58	10/3/2017 5:41	57	11/3/2017 6:46	59	12/3/2017 7:51	57		
7/3/2017 2:31	55	8/3/2017 3:36	55	9/3/2017 4:41	58	10/3/2017 5:46	56	11/3/2017 6:51	59	12/3/2017 7:56	58		
7/3/2017 2:36	55	8/3/2017 3:41	54	9/3/2017 4:46	57	10/3/2017 5:51	58	11/3/2017 6:56	59	13/3/2017 0:01	58		
7/3/2017 2:41	54	8/3/2017 3:46	55	9/3/2017 4:51	58	10/3/2017 5:56	56	11/3/2017 7:01	61	13/3/2017 0:06	57		
7/3/2017 2:46	55	8/3/2017 3:51	54	9/3/2017 4:56	58	10/3/2017 6:01	57	11/3/2017 7:06	59	13/3/2017 0:11	57		
7/3/2017 2:51	54	8/3/2017 3:56	54	9/3/2017 5:01	57	10/3/2017 6:06	57	11/3/2017 7:11	59	13/3/2017 0:16	57		
7/3/2017 2:56	55	8/3/2017 4:01	54	9/3/2017 5:06	58	10/3/2017 6:11	57	11/3/2017 7:16	60	13/3/2017 0:21	57		
7/3/2017 3:01	54	8/3/2017 4:06	54	9/3/2017 5:11	58	10/3/2017 6:16	58	11/3/2017 7:21	59	13/3/2017 0:26	57		
7/3/2017 3:06	54	8/3/2017 4:11	55	9/3/2017 5:16	58	10/3/2017 6:21	57	11/3/2017 7:26	59	13/3/2017 0:31	57		
7/3/2017 3:11	55	8/3/2017 4:16	54	9/3/2017 5:21	58	10/3/2017 6:26	60	11/3/2017 7:31	59	13/3/2017 0:36	57		
7/3/2017 3:16	55	8/3/2017 4:21	55	9/3/2017 5:26	58	10/3/2017 6:31	59	11/3/2017 7:36	58	13/3/2017 0:41	57		
7/3/2017 3:21	55	8/3/2017 4:26	54	9/3/2017 5:31	58	10/3/2017 6:36	60	11/3/2017 7:41	59	13/3/2017 0:46	56		
7/3/2017 3:26	54	8/3/2017 4:31	55	9/3/2017 5:36	58	10/3/2017 6:41	60	11/3/2017 7:46	59	13/3/2017 0:51	57		
7/3/2017 3:31	55	8/3/2017 4:36	55	9/3/2017 5:41	58	10/3/2017 6:46	60	11/3/2017 7:51	59	13/3/2017 0:56	56		
7/3/2017 3:36	55	8/3/2017 4:41	54	9/3/2017 5:46	58	10/3/2017 6:51	61	11/3/2017 7:56	59	13/3/2017 1:01	57		
7/3/2017 3:41	55	8/3/2017 4:46	55	9/3/2017 5:51	59	10/3/2017 6:56	61	12/3/2017 0:01	58	13/3/2017 1:06	56		
7/3/2017 3:46	55	8/3/2017 4:51	55	9/3/2017 5:56	59	10/3/2017 7:01	59	12/3/2017 0:06	58	13/3/2017 1:11	55		
7/3/2017 3:51	55	8/3/2017 4:56	54	9/3/2017 6:01	59	10/3/2017 7:06	59	12/3/2017 0:11	58	13/3/2017 1:16	55		
7/3/2017 3:56	55	8/3/2017 5:01	55	9/3/2017 6:06	59	10/3/2017 7:11	59	12/3/2017 0:16	59	13/3/2017 1:21	55		
7/3/2017 4:01	53	8/3/2017 5:06	54	9/3/2017 6:11	59	10/3/2017 7:16	59	12/3/2017 0:21	58	13/3/2017 1:26	56		
7/3/2017 4:06	55	8/3/2017 5:11	55	9/3/2017 6:16	60	10/3/2017 7:21	59	12/3/2017 0:26	58	13/3/2017 1:31	55		
7/3/2017 4:11	54	8/3/2017 5:16	54	9/3/2017 6:21	60	10/3/2017 7:26	59	12/3/2017 0:31	58	13/3/2017 1:36	55		
7/3/2017 4:16	55	8/3/2017 5:21	55	9/3/2017 6:26	61	10/3/2017 7:31	59	12/3/2017 0:36	58	13/3/2017 1:41	54		
7/3/2017 4:21	55	8/3/2017 5:26	56	9/3/2017 6:31	60	10/3/2017 7:36	59	12/3/2017 0:41	57	13/3/2017 1:46	55		
7/3/2017 4:26	54	8/3/2017 5:31	56	9/3/2017 6:36	48	10/3/2017 7:41	59	12/3/2017 0:46	57	13/3/2017 1:51	56		
7/3/2017 4:31	54	8/3/2017 5:36	56	9/3/2017 6:41	44	10/3/2017 7:46	59	12/3/2017 0:51	57	13/3/2017 1:56	56		
7/3/2017 4:36	55	8/3/2017 5:41	55	9/3/2017 6:46	53	10/3/2017 7:51	59	12/3/2017 0:56	58	13/3/2017 2:01	54		
7/3/2017 4:41	55	8/3/2017 5:46	55	9/3/2017 6:51	61	10/3/2017 7:56	59	12/3/2017 1:01	58	13/3/2017 2:06	55		
7/3/2017 4:46	55	8/3/2017 5:51	57	9/3/2017 6:56	39	11/3/2017 0:01	59	12/3/2017 1:06	58	13/3/2017 2:11	55		
7/3/2017 4:51	55	8/3/2017 5:56	57	9/3/2017 7:01	59	11/3/2017 0:06	58	12/3/2017 1:11	58	13/3/2017 2:16	54		
7/3/2017 4:56	55	8/3/2017 6:01	57	9/3/2017 7:06	59	11/3/2017 0:11	58	12/3/2017 1:16	58	13/3/2017 2:21	55		
7/3/2017 5:01	54	8/3/2017 6:06	57	9/3/2017 7:11	59	11/3/2017 0:16	58	12/3/2017 1:21	58	13/3/2017 2:26	54		
7/3/2017 5:06	55	8/3/2017 6:11	58	9/3/2017 7:16	59	11/3/2017 0:21	57	12/3/2017 1:26	57	13/3/2017 2:31	54		
7/3/2017 5:11	55	8/3/2017 6:16	59	9/3/2017 7:21	59	11/3/2017 0:26	35	12/3/2017 1:31	57	13/3/2017 2:36	54		
7/3/2017 5:16	55	8/3/2017 6:21	58	9/3/2017 7:26	59	11/3/2017 0:31	58	12/3/2017 1:36	57	13/3/2017 2:41	55		
7/3/2017 5:21	56	8/3/2017 6:26	59	9/3/2017 7:31	58	11/3/2017 0:36	59	12/3/2017 1:41	58	13/3/2017 2:46	56		
7/3/2017 5:26	55	8/3/2017 6:31	60	9/3/2017 7:36	58	11/3/2017 0:41	58	12/3/2017 1:46	57	13/3/2017 2:51	53		
7/3/2017 5:31	56	8/3/2017 6:36	60	9/									

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)							
13/3/2017 5:56	56	14/3/2017 23:01	60	16/3/2017 0:06	58	17/3/2017 1:11	57	18/3/2017 2:16	56
13/3/2017 6:01	57	14/3/2017 23:06	59	16/3/2017 0:11	58	17/3/2017 1:16	56	18/3/2017 2:21	57
13/3/2017 6:06	57	14/3/2017 23:11	59	16/3/2017 0:16	58	17/3/2017 1:21	56	18/3/2017 2:26	56
13/3/2017 6:11	58	14/3/2017 23:16	59	16/3/2017 0:21	58	17/3/2017 1:26	56	18/3/2017 2:31	57
13/3/2017 6:16	58	14/3/2017 23:21	60	16/3/2017 0:26	59	17/3/2017 1:31	60	18/3/2017 2:36	56
13/3/2017 6:21	58	14/3/2017 23:26	60	16/3/2017 0:31	59	17/3/2017 1:36	57	18/3/2017 2:41	56
13/3/2017 6:26	60	14/3/2017 23:31	59	16/3/2017 0:36	58	17/3/2017 1:41	55	18/3/2017 2:46	58
13/3/2017 6:31	59	14/3/2017 23:36	59	16/3/2017 0:41	58	17/3/2017 1:46	56	18/3/2017 2:51	56
13/3/2017 6:36	60	14/3/2017 23:41	59	16/3/2017 0:46	58	17/3/2017 1:51	56	18/3/2017 2:56	56
13/3/2017 6:41	61	14/3/2017 23:46	59	16/3/2017 0:51	58	17/3/2017 1:56	56	18/3/2017 3:01	56
13/3/2017 6:46	60	14/3/2017 23:51	59	16/3/2017 0:56	57	17/3/2017 2:01	55	18/3/2017 3:06	56
13/3/2017 6:51	60	14/3/2017 23:56	58	16/3/2017 1:01	57	17/3/2017 2:06	56	18/3/2017 3:11	57
13/3/2017 6:56	59	15/3/2017 0:01	59	16/3/2017 1:06	57	17/3/2017 2:11	55	18/3/2017 3:16	56
13/3/2017 23:01	60	15/3/2017 0:06	58	16/3/2017 1:11	57	17/3/2017 2:16	56	18/3/2017 3:21	56
13/3/2017 23:06	59	15/3/2017 0:11	58	16/3/2017 1:16	56	17/3/2017 2:21	57	18/3/2017 3:26	55
13/3/2017 23:11	59	15/3/2017 0:16	58	16/3/2017 1:21	56	17/3/2017 2:26	55	18/3/2017 3:31	56
13/3/2017 23:16	59	15/3/2017 0:21	59	16/3/2017 1:26	57	17/3/2017 2:31	55	18/3/2017 3:36	56
13/3/2017 23:21	59	15/3/2017 0:26	58	16/3/2017 1:31	56	17/3/2017 2:36	56	18/3/2017 3:41	56
13/3/2017 23:26	58	15/3/2017 0:31	58	16/3/2017 1:36	57	17/3/2017 2:41	55	18/3/2017 3:46	56
13/3/2017 23:31	58	15/3/2017 0:36	58	16/3/2017 1:41	57	17/3/2017 2:46	56	18/3/2017 3:51	56
13/3/2017 23:36	59	15/3/2017 0:41	57	16/3/2017 1:46	56	17/3/2017 2:51	56	18/3/2017 3:56	56
13/3/2017 23:41	59	15/3/2017 0:46	57	16/3/2017 1:51	56	17/3/2017 2:56	56	18/3/2017 4:01	55
13/3/2017 23:46	60	15/3/2017 0:51	57	16/3/2017 1:56	56	17/3/2017 3:01	55	18/3/2017 4:06	56
13/3/2017 23:51	58	15/3/2017 0:56	57	16/3/2017 2:01	56	17/3/2017 3:06	55	18/3/2017 4:11	55
13/3/2017 23:56	58	15/3/2017 1:01	58	16/3/2017 2:06	55	17/3/2017 3:11	54	18/3/2017 4:16	56
14/3/2017 0:01	58	15/3/2017 1:06	56	16/3/2017 2:11	56	17/3/2017 3:16	55	18/3/2017 4:21	57
14/3/2017 0:06	58	15/3/2017 1:11	57	16/3/2017 2:16	55	17/3/2017 3:21	55	18/3/2017 4:26	56
14/3/2017 0:11	57	15/3/2017 1:16	58	16/3/2017 2:21	55	17/3/2017 3:26	55	18/3/2017 4:31	55
14/3/2017 0:16	58	15/3/2017 1:21	57	16/3/2017 2:26	56	17/3/2017 3:31	54	18/3/2017 4:36	55
14/3/2017 0:21	57	15/3/2017 1:26	56	16/3/2017 2:31	56	17/3/2017 3:36	55	18/3/2017 4:41	56
14/3/2017 0:26	57	15/3/2017 1:31	57	16/3/2017 2:36	56	17/3/2017 3:41	54	18/3/2017 4:46	55
14/3/2017 0:31	57	15/3/2017 1:36	56	16/3/2017 2:41	55	17/3/2017 3:46	55	18/3/2017 4:51	56
14/3/2017 0:36	57	15/3/2017 1:41	56	16/3/2017 2:46	57	17/3/2017 3:51	55	18/3/2017 4:56	55
14/3/2017 0:41	58	15/3/2017 1:46	56	16/3/2017 2:51	55	17/3/2017 3:56	54	18/3/2017 5:01	55
14/3/2017 0:46	57	15/3/2017 1:51	57	16/3/2017 2:56	55	17/3/2017 4:01	54	18/3/2017 5:06	56
14/3/2017 0:51	57	15/3/2017 1:56	57	16/3/2017 3:01	55	17/3/2017 4:06	56	18/3/2017 5:11	55
14/3/2017 0:56	57	15/3/2017 2:01	56	16/3/2017 3:06	55	17/3/2017 4:11	54	18/3/2017 5:16	56
14/3/2017 1:01	58	15/3/2017 2:06	56	16/3/2017 3:11	55	17/3/2017 4:16	55	18/3/2017 5:21	56
14/3/2017 1:06	56	15/3/2017 2:11	56	16/3/2017 3:16	56	17/3/2017 4:21	54	18/3/2017 5:26	56
14/3/2017 1:11	56	15/3/2017 2:16	57	16/3/2017 3:21	55	17/3/2017 4:26	55	18/3/2017 5:31	56
14/3/2017 1:16	56	15/3/2017 2:21	57	16/3/2017 3:26	56	17/3/2017 4:31	53	18/3/2017 5:36	56
14/3/2017 1:21	58	15/3/2017 2:26	56	16/3/2017 3:31	56	17/3/2017 4:36	55	18/3/2017 5:41	56
14/3/2017 1:26	57	15/3/2017 2:31	56	16/3/2017 3:36	54	17/3/2017 4:41	54	18/3/2017 5:46	56
14/3/2017 1:31	56	15/3/2017 2:36	56	16/3/2017 3:41	54	17/3/2017 4:46	54	18/3/2017 5:51	57
14/3/2017 1:36	57	15/3/2017 2:41	55	16/3/2017 3:46	58	17/3/2017 4:51	55	18/3/2017 5:56	57
14/3/2017 1:41	57	15/3/2017 2:46	55	16/3/2017 3:51	54	17/3/2017 4:56	55	18/3/2017 6:01	57
14/3/2017 1:46	57	15/3/2017 2:51	56	16/3/2017 3:56	55	17/3/2017 5:01	55	18/3/2017 6:06	57
14/3/2017 1:51	57	15/3/2017 2:56	56	16/3/2017 4:01	54	17/3/2017 5:06	55	18/3/2017 6:11	59
14/3/2017 1:56	57	15/3/2017 3:01	55	16/3/2017 4:06	55	17/3/2017 5:11	54	18/3/2017 6:16	58
14/3/2017 2:01	56	15/3/2017 3:06	55	16/3/2017 4:11	55	17/3/2017 5:16	55	18/3/2017 6:21	57
14/3/2017 2:06	56	15/3/2017 3:11	55	16/3/2017 4:16	55	17/3/2017 5:21	56	18/3/2017 6:26	59
14/3/2017 2:11	56	15/3/2017 3:16	54	16/3/2017 4:21	55	17/3/2017 5:26	56	18/3/2017 6:31	58
14/3/2017 2:16	56	15/3/2017 3:21	56	16/3/2017 4:26	55	17/3/2017 5:31	55	18/3/2017 6:36	59
14/3/2017 2:21	55	15/3/2017 3:26	56	16/3/2017 4:31	55	17/3/2017 5:36	56	18/3/2017 6:41	59
14/3/2017 2:26	56	15/3/2017 3:31	55	16/3/2017 4:36	54	17/3/2017 5:41	58	18/3/2017 6:46	59
14/3/2017 2:31	56	15/3/2017 3:36	56	16/3/2017 4:41	54	17/3/2017 5:46	56	18/3/2017 6:51	59
14/3/2017 2:36	56	15/3/2017 3:41	55	16/3/2017 4:46	55	17/3/2017 5:51	57	18/3/2017 6:56	59
14/3/2017 2:41	56	15/3/2017 3:46	56	16/3/2017 4:51	54	17/3/2017 5:56	57	18/3/2017 7:01	60
14/3/2017 2:46	56	15/3/2017 3:51	55	16/3/2017 4:56	55	17/3/2017 6:01	57	18/3/2017 7:06	60
14/3/2017 2:51	56	15/3/2017 3:56	55	16/3/2017 5:01	55	17/3/2017 6:06	59	18/3/2017 7:11	59
14/3/2017 2:56	56	15/3/2017 4:01	56	16/3/2017 5:06	55	17/3/2017 6:11	59	18/3/2017 7:16	59
14/3/2017 3:01	56	15/3/2017 4:06	56	16/3/2017 5:11	56	17/3/2017 6:16	59	18/3/2017 7:21	59
14/3/2017 3:06	56	15/3/2017 4:11	56	16/3/2017 5:16	54	17/3/2017 6:21	58	18/3/2017 7:26	59
14/3/2017 3:11	56	15/3/2017 4:16	55	16/3/2017 5:21	55	17/3/2017 6:26	59	18/3/2017 7:31	60
14/3/2017 3:16	56	15/3/2017 4:21	55	16/3/2017 5:26	56	17/3/2017 6:31	60	18/3/2017 7:36	60
14/3/2017 3:21	55	15/3/2017 4:26	56	16/3/2017 5:31	56	17/3/2017 6:36	60	18/3/2017 7:41	59
14/3/2017 3:26	56	15/3/2017 4:31	55	16/3/2017 5:36	56	17/3/2017 6:41	61	18/3/2017 7:46	59
14/3/2017 3:31	57	15/3/2017 4:36	56	16/3/2017 5:41	56	17/3/2017 6:46	60	18/3/2017 7:51	58
14/3/2017 3:36	56	15/3/2017 4:41	55	16/3/2017 5:46	56	17/3/2017 6:51	61	18/3/2017 7:56	59
14/3/2017 3:41	55	15/3/2017 4:46	55	16/3/2017 5:51	57	17/3/2017 6:56	47	18/3/2017 8:01	58
14/3/2017 3:46	56	15/3/2017 4:51	56	16/3/2017 5:56	57	17/3/2017 7:01	57	18/3/2017 8:06	59
14/3/2017 3:51	55	15/3/2017 4:56	56	16/3/2017 6:01	57	17/3/2017 7:06	60	18/3/2017 8:11	59
14/3/2017 3:56	55	15/3/2017 5:01	55	16/3/2017 6:06	58	17/3/2017 7:11	60	18/3/2017 8:16	59
14/3/2017 4:01	55	15/3/2017 5:06	56	16/3/2017 6:11	58	17/3/2017 7:16	60	18/3/2017 8:21	59
14/3/2017 4:06	56	15/3/2017 5:11	56	16/3/2017 6:16	58	17/3/2017 7:21	59	18/3/2017 8:26	59
14/3/2017 4:11	55	15/3/2017 5:16	55	16/3/2017 6:21	59	17/3/2017 7:26	59	18/3/2017 8:31	59
14/3/2017 4:16	56	15/3/2017 5:21	58	16/3/2017 6:26	59	17/3/2017 7:31	59	18/3/2017 8:36	58
14/3/2017 4:21	56	15/3/2017 5:26	57	16/3/2017 6:31	59	17/3/2017 7:36	58	18/3/2017 8:41	57
14/3/2017 4:26	54	15/3/2017 5:31	56	16/3/2017 6:36	60	17/3/2017 7:41	60	18/3/2017 8:46	58
14/3/2017 4:31	55	15/3/2017 5:36	57	16/3/2017 6:41	61	17/3/2017 7:46	59	18/3/2017 8:51	57
14/3/2017 4:36	56	15/3/2017 5:41	56	16/3/2017 6:46	61	17/3/2017 7:51	59	18/3/2017 8:56	58
14/3/2017 4:41	54	15/3/2017 5:46	58	16/3/2017 6:51	61	17/3/2017 7:56	59	18/3/2017 9:01	57
14/3/2017 4:46	55	15/3/2017 5:51	58	16/3/2017 6:56	59	18/3/2017 0:01	59	18/3/2017 9:06	59
14/3/2017 4:51	55	15/3/2017 5:56	58	16/3/2017 7:01	59	18/3/2017 0:06	58	18/3/2017 9:11	57
14/3/2017 4:56	55	15/3/2017 6:01	57	16/3/2017 7:06	59	18/3/2017 0:11	59	18/3/2017 9:16	58
14/3/2017 5:01	56	15/3/2017 6:06	58	16/3/2017 7:11	60	18/3/2017 0:16	59	18/3/2017 9:21	57
14/3/2017 5:06	56	15/3/2017 6:11	58	16/3/2017 7:16	59	18/3/2017 0:21	58	18/3/2017 9:26	57
14/3/2017 5:11	56	15/3/2017 6:16	59	16/3/2017 7:21	59	18/3/2017 0:26	58	18/3/2017 9:31	56
14/3/2017 5:16	56	15/3/2017 6:21	58	16/3/2017 7:26	59	18/3/2017 0:31	59	18/3/2017 9:36	56
14/3/2017 5:21	56	15/3/2017 6:26	60	16/3/2017 7:31	59	18/3/2017 0:36	58	18/3/2017 9:41	57
14/3/2017 5:26	56	15/3/2017 6:31	60						

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)							
20/3/2017 4:26	55	21/3/2017 5:31	56	22/3/2017 6:36	60	23/3/2017 23:41	59	25/3/2017 0:46	57
20/3/2017 4:31	54	21/3/2017 5:36	57	22/3/2017 6:41	43	23/3/2017 23:46	59	25/3/2017 0:51	58
20/3/2017 4:36	54	21/3/2017 5:41	57	22/3/2017 6:46	60	23/3/2017 23:51	58	25/3/2017 0:56	57
20/3/2017 4:41	55	21/3/2017 5:46	57	22/3/2017 6:51	60	23/3/2017 23:56	59	25/3/2017 1:01	58
20/3/2017 4:46	56	21/3/2017 5:51	58	22/3/2017 6:56	59	24/3/2017 0:01	57	25/3/2017 1:06	57
20/3/2017 4:51	53	21/3/2017 5:56	58	22/3/2017 23:01	59	24/3/2017 0:06	58	25/3/2017 1:11	57
20/3/2017 4:56	55	21/3/2017 6:01	57	22/3/2017 23:06	58	24/3/2017 0:11	58	25/3/2017 1:16	58
20/3/2017 5:01	55	21/3/2017 6:06	58	22/3/2017 23:11	59	24/3/2017 0:16	58	25/3/2017 1:21	58
20/3/2017 5:06	55	21/3/2017 6:11	59	22/3/2017 23:16	59	24/3/2017 0:21	58	25/3/2017 1:26	57
20/3/2017 5:11	55	21/3/2017 6:16	59	22/3/2017 23:21	59	24/3/2017 0:26	57	25/3/2017 1:31	57
20/3/2017 5:16	55	21/3/2017 6:21	60	22/3/2017 23:26	59	24/3/2017 0:31	58	25/3/2017 1:36	58
20/3/2017 5:21	56	21/3/2017 6:26	41	22/3/2017 23:31	59	24/3/2017 0:36	58	25/3/2017 1:41	57
20/3/2017 5:26	55	21/3/2017 6:31	56	22/3/2017 23:36	59	24/3/2017 0:41	58	25/3/2017 1:46	58
20/3/2017 5:31	56	21/3/2017 6:36	61	22/3/2017 23:41	58	24/3/2017 0:46	58	25/3/2017 1:51	58
20/3/2017 5:36	56	21/3/2017 6:41	55	22/3/2017 23:46	58	24/3/2017 0:51	57	25/3/2017 1:56	57
20/3/2017 5:41	57	21/3/2017 6:46	59	22/3/2017 23:51	58	24/3/2017 0:56	58	25/3/2017 2:01	56
20/3/2017 5:46	56	21/3/2017 6:51	56	22/3/2017 23:56	58	24/3/2017 1:01	56	25/3/2017 2:06	56
20/3/2017 5:51	58	21/3/2017 6:56	61	23/3/2017 0:01	58	24/3/2017 1:06	57	25/3/2017 2:11	57
20/3/2017 5:56	57	21/3/2017 23:01	58	23/3/2017 0:06	58	24/3/2017 1:11	57	25/3/2017 2:16	57
20/3/2017 6:01	57	21/3/2017 23:06	59	23/3/2017 0:11	57	24/3/2017 1:16	58	25/3/2017 2:21	56
20/3/2017 6:06	58	21/3/2017 23:11	59	23/3/2017 0:16	57	24/3/2017 1:21	57	25/3/2017 2:26	57
20/3/2017 6:11	59	21/3/2017 23:16	59	23/3/2017 0:21	57	24/3/2017 1:26	56	25/3/2017 2:31	56
20/3/2017 6:16	59	21/3/2017 23:21	58	23/3/2017 0:26	57	24/3/2017 1:31	57	25/3/2017 2:36	57
20/3/2017 6:21	59	21/3/2017 23:26	59	23/3/2017 0:31	58	24/3/2017 1:36	57	25/3/2017 2:41	57
20/3/2017 6:26	60	21/3/2017 23:31	59	23/3/2017 0:36	58	24/3/2017 1:41	56	25/3/2017 2:46	57
20/3/2017 6:31	60	21/3/2017 23:36	58	23/3/2017 0:41	58	24/3/2017 1:46	56	25/3/2017 2:51	57
20/3/2017 6:36	61	21/3/2017 23:41	59	23/3/2017 0:46	57	24/3/2017 1:51	55	25/3/2017 2:56	56
20/3/2017 6:41	47	21/3/2017 23:46	59	23/3/2017 0:51	57	24/3/2017 1:56	56	25/3/2017 3:01	56
20/3/2017 6:46	61	21/3/2017 23:51	58	23/3/2017 0:56	57	24/3/2017 2:01	55	25/3/2017 3:06	57
20/3/2017 6:51	49	21/3/2017 23:56	59	23/3/2017 1:01	58	24/3/2017 2:06	55	25/3/2017 3:11	57
20/3/2017 6:56	61	22/3/2017 0:01	57	23/3/2017 1:06	57	24/3/2017 2:11	55	25/3/2017 3:16	55
20/3/2017 23:01	60	22/3/2017 0:06	58	23/3/2017 1:11	57	24/3/2017 2:16	54	25/3/2017 3:21	56
20/3/2017 23:06	60	22/3/2017 0:11	58	23/3/2017 1:16	57	24/3/2017 2:21	55	25/3/2017 3:26	57
20/3/2017 23:11	60	22/3/2017 0:16	58	23/3/2017 1:21	55	24/3/2017 2:26	55	25/3/2017 3:31	56
20/3/2017 23:16	59	22/3/2017 0:21	58	23/3/2017 1:26	56	24/3/2017 2:31	55	25/3/2017 3:36	56
20/3/2017 23:21	60	22/3/2017 0:26	58	23/3/2017 1:31	56	24/3/2017 2:36	55	25/3/2017 3:41	57
20/3/2017 23:26	59	22/3/2017 0:31	58	23/3/2017 1:36	57	24/3/2017 2:41	55	25/3/2017 3:46	57
20/3/2017 23:31	59	22/3/2017 0:36	57	23/3/2017 1:41	56	24/3/2017 2:46	55	25/3/2017 3:51	56
20/3/2017 23:36	59	22/3/2017 0:41	56	23/3/2017 1:46	56	24/3/2017 2:51	54	25/3/2017 3:56	56
20/3/2017 23:41	58	22/3/2017 0:46	57	23/3/2017 1:51	57	24/3/2017 2:56	55	25/3/2017 4:01	56
20/3/2017 23:46	59	22/3/2017 0:51	57	23/3/2017 1:56	57	24/3/2017 3:01	54	25/3/2017 4:06	56
20/3/2017 23:51	59	22/3/2017 0:56	57	23/3/2017 2:01	55	24/3/2017 3:06	54	25/3/2017 4:11	56
20/3/2017 23:56	59	22/3/2017 1:01	57	23/3/2017 2:06	56	24/3/2017 3:11	55	25/3/2017 4:16	57
21/3/2017 0:01	58	22/3/2017 1:06	57	23/3/2017 2:11	56	24/3/2017 3:16	54	25/3/2017 4:21	56
21/3/2017 0:06	58	22/3/2017 1:11	57	23/3/2017 2:16	56	24/3/2017 3:21	55	25/3/2017 4:26	57
21/3/2017 0:11	58	22/3/2017 1:16	57	23/3/2017 2:21	56	24/3/2017 3:26	54	25/3/2017 4:31	56
21/3/2017 0:16	59	22/3/2017 1:21	57	23/3/2017 2:26	56	24/3/2017 3:31	54	25/3/2017 4:36	55
21/3/2017 0:21	59	22/3/2017 1:26	57	23/3/2017 2:31	56	24/3/2017 3:36	56	25/3/2017 4:41	55
21/3/2017 0:26	58	22/3/2017 1:31	57	23/3/2017 2:36	56	24/3/2017 3:41	55	25/3/2017 4:46	54
21/3/2017 0:31	58	22/3/2017 1:36	57	23/3/2017 2:41	57	24/3/2017 3:46	54	25/3/2017 4:51	55
21/3/2017 0:36	58	22/3/2017 1:41	56	23/3/2017 2:46	55	24/3/2017 3:51	55	25/3/2017 4:56	56
21/3/2017 0:41	58	22/3/2017 1:46	56	23/3/2017 2:51	56	24/3/2017 3:56	54	25/3/2017 5:01	56
21/3/2017 0:46	58	22/3/2017 1:51	56	23/3/2017 2:56	55	24/3/2017 4:01	56	25/3/2017 5:06	55
21/3/2017 0:51	58	22/3/2017 1:56	55	23/3/2017 3:01	55	24/3/2017 4:06	55	25/3/2017 5:11	56
21/3/2017 0:56	57	22/3/2017 2:01	55	23/3/2017 3:06	56	24/3/2017 4:11	56	25/3/2017 5:16	55
21/3/2017 1:01	57	22/3/2017 2:06	55	23/3/2017 3:11	56	24/3/2017 4:16	54	25/3/2017 5:21	56
21/3/2017 1:06	59	22/3/2017 2:11	55	23/3/2017 3:16	55	24/3/2017 4:21	54	25/3/2017 5:26	56
21/3/2017 1:11	58	22/3/2017 2:16	55	23/3/2017 3:21	54	24/3/2017 4:26	55	25/3/2017 5:31	57
21/3/2017 1:16	57	22/3/2017 2:21	55	23/3/2017 3:26	55	24/3/2017 4:31	55	25/3/2017 5:36	56
21/3/2017 1:21	57	22/3/2017 2:26	56	23/3/2017 3:31	55	24/3/2017 4:36	55	25/3/2017 5:41	56
21/3/2017 1:26	58	22/3/2017 2:31	56	23/3/2017 3:36	55	24/3/2017 4:41	56	25/3/2017 5:46	56
21/3/2017 1:31	58	22/3/2017 2:36	56	23/3/2017 3:41	55	24/3/2017 4:46	54	25/3/2017 5:51	57
21/3/2017 1:36	58	22/3/2017 2:41	56	23/3/2017 3:46	55	24/3/2017 4:51	55	25/3/2017 5:56	58
21/3/2017 1:41	58	22/3/2017 2:46	55	23/3/2017 3:51	55	24/3/2017 4:56	55	25/3/2017 6:01	57
21/3/2017 1:46	56	22/3/2017 2:51	55	23/3/2017 3:56	55	24/3/2017 5:01	55	25/3/2017 6:06	57
21/3/2017 1:51	57	22/3/2017 2:56	54	23/3/2017 4:01	55	24/3/2017 5:06	56	25/3/2017 6:11	58
21/3/2017 1:56	57	22/3/2017 3:01	55	23/3/2017 4:06	55	24/3/2017 5:11	55	25/3/2017 6:16	58
21/3/2017 2:01	58	22/3/2017 3:06	54	23/3/2017 4:11	56	24/3/2017 5:16	55	25/3/2017 6:21	58
21/3/2017 2:06	57	22/3/2017 3:11	54	23/3/2017 4:16	54	24/3/2017 5:21	56	25/3/2017 6:26	59
21/3/2017 2:11	56	22/3/2017 3:16	56	23/3/2017 4:21	56	24/3/2017 5:26	56	25/3/2017 6:31	59
21/3/2017 2:16	56	22/3/2017 3:21	54	23/3/2017 4:26	56	24/3/2017 5:31	56	25/3/2017 6:36	60
21/3/2017 2:21	57	22/3/2017 3:26	55	23/3/2017 4:31	55	24/3/2017 5:36	56	25/3/2017 6:41	60
21/3/2017 2:26	58	22/3/2017 3:31	54	23/3/2017 4:36	55	24/3/2017 5:41	56	25/3/2017 6:46	60
21/3/2017 2:31	58	22/3/2017 3:36	55	23/3/2017 4:41	55	24/3/2017 5:46	57	25/3/2017 6:51	59
21/3/2017 2:36	57	22/3/2017 3:41	55	23/3/2017 4:46	54	24/3/2017 5:51	57	25/3/2017 6:56	59
21/3/2017 2:41	55	22/3/2017 3:46	56	23/3/2017 4:51	55	24/3/2017 5:56	57	25/3/2017 23:01	59
21/3/2017 2:46	56	22/3/2017 3:51	55	23/3/2017 4:56	56	24/3/2017 6:01	58	25/3/2017 23:06	59
21/3/2017 2:51	57	22/3/2017 3:56	55	23/3/2017 5:01	55	24/3/2017 6:06	58	25/3/2017 23:11	59
21/3/2017 2:56	57	22/3/2017 4:01	55	23/3/2017 5:06	54	24/3/2017 6:11	58	25/3/2017 23:16	59
21/3/2017 3:01	56	22/3/2017 4:06	54	23/3/2017 5:11	55	24/3/2017 6:16	59	25/3/2017 23:21	59
21/3/2017 3:06	56	22/3/2017 4:11	54	23/3/2017 5:16	56	24/3/2017 6:21	59	25/3/2017 23:26	59
21/3/2017 3:11	56	22/3/2017 4:16	55	23/3/2017 5:21	55	24/3/2017 6:26	60	25/3/2017 23:31	58
21/3/2017 3:16	56	22/3/2017 4:21	55	23/3/2017 5:26	56	24/3/2017 6:31	60	25/3/2017 23:36	59
21/3/2017 3:21	56	22/3/2017 4:26	56	23/3/2017 5:31	57	24/3/2017 6:36	60	25/3/2017 23:41	59
21/3/2017 3:26	56	22/3/2017 4:31	56	23/3/2017 5:36	56	24/3/2017 6:41	45	25/3/2017 23:46	58
21/3/2017 3:31	56	22/3/2017 4:36	55	23/3/2017 5:41	56	24/3/2017 6:46	61	25/3/2017 23:51	59
21/3/2017 3:36	56	22/3/2017 4:41	55	23/3/2017 5:46	57	24/3/2017 6:51	60	25/3/2017 23:56	59
21/3/2017 3:41	55	22/3/2017 4:46	54	23/3/2017 5:51	57	24/3/2017 6:56	60	26/3/2017 0:01	59
21/3/2017 3:46	55	22/3/2017 4:51	54	23/3/2017 5:56	57	24/3/2017 23:01	61	26/3/2017 0:06	59
21/3/2017 3:51	56	22/3/2017 4:56	55	23/3/2017 6:01	57	24/3/2017 23:06	60	26/3/2017 0:11	58
21/3/2017 3:56									

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
Normal Day 07:00-19:00		31/3/2017 12:31	67	7/4/2017 7:01	64	12/4/2017 13:31	69	21/4/2017 8:01	68	26/4/2017 14:31	66
27/3/2017 7:01	64	31/3/2017 13:01	68	7/4/2017 7:31	65	12/4/2017 14:01	67	21/4/2017 8:31	70	26/4/2017 15:01	66
27/3/2017 7:31	65	31/3/2017 13:31	68	7/4/2017 8:01	66	12/4/2017 14:31	66	21/4/2017 9:01	66	26/4/2017 15:31	66
27/3/2017 8:01	65	31/3/2017 14:01	67	7/4/2017 8:31	65	12/4/2017 15:01	66	21/4/2017 9:31	66	26/4/2017 16:01	66
27/3/2017 8:31	65	31/3/2017 14:31	67	7/4/2017 9:01	65	12/4/2017 15:31	67	21/4/2017 10:01	69	26/4/2017 16:31	66
27/3/2017 9:01	66	31/3/2017 15:01	66	7/4/2017 9:31	65	12/4/2017 16:01	68	21/4/2017 10:31	67	26/4/2017 17:01	67
27/3/2017 9:31	67	31/3/2017 15:31	66	7/4/2017 10:01	65	12/4/2017 16:31	68	21/4/2017 11:01	66	26/4/2017 17:31	67
27/3/2017 10:01	67	31/3/2017 16:01	66	7/4/2017 10:31	66	12/4/2017 17:01	67	21/4/2017 11:31	66	26/4/2017 18:01	66
27/3/2017 10:31	67	31/3/2017 16:31	66	7/4/2017 11:01	66	12/4/2017 17:31	66	21/4/2017 12:01	66	26/4/2017 18:31	66
27/3/2017 11:01	67	31/3/2017 17:01	66	7/4/2017 11:31	66	12/4/2017 18:01	66	21/4/2017 12:31	66		
27/3/2017 11:31	66	31/3/2017 17:31	66	7/4/2017 12:01	65	12/4/2017 18:31	66	21/4/2017 13:01	67	<u>Normal Day 19:00-23:00</u> <u>Sunday & Holiday</u> <u>07:00-23:00</u>	
27/3/2017 12:01	66	31/3/2017 18:01	66	7/4/2017 12:31	65	13/4/2017 7:01	65	21/4/2017 13:31	66		
27/3/2017 12:31	66	31/3/2017 18:31	65	7/4/2017 13:01	66	13/4/2017 7:31	67	21/4/2017 14:01	66	27/3/2017 19:01	65
27/3/2017 13:01	67	1/4/2017 7:01	64	7/4/2017 13:31	66	13/4/2017 8:01	67	21/4/2017 14:31	66	27/3/2017 19:31	66
27/3/2017 13:31	66	1/4/2017 7:31	66	7/4/2017 14:01	66	13/4/2017 8:31	65	21/4/2017 15:01	66	27/3/2017 19:51	63
27/3/2017 14:01	66	1/4/2017 8:01	67	7/4/2017 14:31	66	13/4/2017 9:01	65	21/4/2017 15:31	66	27/3/2017 19:56	63
27/3/2017 14:31	66	1/4/2017 8:31	67	7/4/2017 15:01	66	13/4/2017 9:31	67	21/4/2017 16:01	72	27/3/2017 20:01	64
27/3/2017 15:01	67	1/4/2017 9:01	67	7/4/2017 15:31	66	13/4/2017 10:01	69	21/4/2017 16:31	69	27/3/2017 20:06	64
27/3/2017 15:31	66	1/4/2017 9:31	67	7/4/2017 16:01	66	13/4/2017 10:31	67	21/4/2017 17:01	67	27/3/2017 20:11	64
27/3/2017 16:01	66	1/4/2017 10:01	66	7/4/2017 16:31	66	13/4/2017 11:01	67	21/4/2017 17:31	66	27/3/2017 20:16	64
27/3/2017 16:31	66	1/4/2017 10:31	66	7/4/2017 17:01	66	13/4/2017 11:31	67	21/4/2017 18:01	66	27/3/2017 20:21	64
27/3/2017 17:01	67	1/4/2017 11:01	66	7/4/2017 17:31	66	13/4/2017 12:01	67	21/4/2017 18:31	64	27/3/2017 20:26	64
27/3/2017 17:31	66	1/4/2017 11:31	66	7/4/2017 18:01	67	13/4/2017 12:31	66	21/4/2017 19:01	63	27/3/2017 20:31	64
27/3/2017 18:01	66	1/4/2017 12:01	66	7/4/2017 18:31	66	13/4/2017 13:01	67	21/4/2017 19:31	65	27/3/2017 20:36	63
27/3/2017 18:31	66	1/4/2017 12:31	66	7/4/2017 19:01	67	13/4/2017 13:31	67	21/4/2017 19:51	63	27/3/2017 20:41	63
27/3/2017 19:01	65	1/4/2017 13:01	66	7/4/2017 19:31	67	13/4/2017 14:01	67	21/4/2017 20:01	66	27/3/2017 20:46	63
27/3/2017 19:31	65	1/4/2017 13:31	65	7/4/2017 20:01	66	13/4/2017 14:31	66	21/4/2017 20:11	66	27/3/2017 20:51	63
27/3/2017 20:01	65	1/4/2017 14:01	65	7/4/2017 20:31	66	13/4/2017 15:01	66	21/4/2017 20:16	64	27/3/2017 20:56	63
27/3/2017 20:31	65	1/4/2017 14:31	66	7/4/2017 21:01	66	13/4/2017 15:31	66	21/4/2017 20:21	64	27/3/2017 21:01	64
27/3/2017 21:01	65	1/4/2017 15:01	66	7/4/2017 21:31	66	13/4/2017 16:01	67	21/4/2017 20:26	64	27/3/2017 21:06	64
27/3/2017 21:31	65	1/4/2017 15:31	65	7/4/2017 22:01	66	13/4/2017 16:31	66	21/4/2017 20:31	64	27/3/2017 21:11	64
27/3/2017 22:01	65	1/4/2017 16:01	66	7/4/2017 22:31	66	13/4/2017 17:01	66	21/4/2017 20:36	63	27/3/2017 21:16	63
27/3/2017 22:31	65	1/4/2017 16:31	65	7/4/2017 23:01	66	13/4/2017 17:31	66	21/4/2017 20:41	63	27/3/2017 21:21	63
27/3/2017 23:01	66	1/4/2017 17:01	66	7/4/2017 23:31	66	13/4/2017 18:01	66	21/4/2017 20:46	63	27/3/2017 21:26	63
27/3/2017 23:31	66	1/4/2017 17:31	66	7/4/2017 24:01	66	13/4/2017 18:31	66	21/4/2017 20:51	63	27/3/2017 21:31	63
27/3/2017 24:01	66	1/4/2017 18:01	66	7/4/2017 24:31	66	13/4/2017 19:01	66	21/4/2017 20:56	63	27/3/2017 21:36	63
27/3/2017 24:31	66	1/4/2017 18:31	66	7/4/2017 25:01	66	13/4/2017 19:31	66	21/4/2017 21:01	64	27/3/2017 21:41	64
27/3/2017 25:01	66	1/4/2017 19:01	66	7/4/2017 25:31	66	13/4/2017 20:01	67	21/4/2017 21:06	64	27/3/2017 21:46	63
27/3/2017 25:31	66	1/4/2017 19:31	65	7/4/2017 26:01	66	13/4/2017 20:31	67	21/4/2017 21:11	64	27/3/2017 21:51	64
27/3/2017 26:01	66	1/4/2017 20:01	66	7/4/2017 26:31	66	13/4/2017 21:01	66	21/4/2017 21:16	63	27/3/2017 21:56	63
27/3/2017 26:31	66	1/4/2017 20:31	66	7/4/2017 27:01	66	13/4/2017 21:31	66	21/4/2017 21:21	63	27/3/2017 22:01	62
27/3/2017 27:01	66	1/4/2017 21:01	66	7/4/2017 27:31	66	13/4/2017 22:01	66	21/4/2017 21:26	63	27/3/2017 22:06	63
27/3/2017 27:31	66	1/4/2017 21:31	66	7/4/2017 28:01	66	13/4/2017 22:31	66	21/4/2017 21:31	63	27/3/2017 22:11	64
27/3/2017 28:01	66	1/4/2017 22:01	66	7/4/2017 28:31	66	13/4/2017 23:01	66	21/4/2017 21:36	63	27/3/2017 22:16	64
27/3/2017 28:31	66	1/4/2017 22:31	66	7/4/2017 29:01	66	13/4/2017 23:31	66	21/4/2017 21:41	64	27/3/2017 22:21	63
27/3/2017 29:01	65	1/4/2017 23:01	66	7/4/2017 29:31	66	13/4/2017 24:01	66	21/4/2017 21:46	63	27/3/2017 22:26	63
27/3/2017 29:31	65	1/4/2017 23:31	66	7/4/2017 30:01	66	13/4/2017 24:31	66	21/4/2017 21:51	64	27/3/2017 22:31	63
27/3/2017 30:01	66	1/4/2017 24:01	66	7/4/2017 30:31	66	13/4/2017 25:01	66	21/4/2017 21:56	63	27/3/2017 22:36	63
27/3/2017 30:31	66	1/4/2017 24:31	66	7/4/2017 31:01	66	13/4/2017 25:31	66	21/4/2017 22:01	66	27/3/2017 22:41	63
27/3/2017 31:01	66	1/4/2017 25:01	66	7/4/2017 31:31	66	13/4/2017 26:01	66	21/4/2017 22:06	64	27/3/2017 22:46	63
27/3/2017 31:31	66	1/4/2017 25:31	66	7/4/2017 32:01	66	13/4/2017 26:31	66	21/4/2017 22:11	64	27/3/2017 22:51	63
27/3/2017 32:01	66	1/4/2017 26:01	66	7/4/2017 32:31	66	13/4/2017 27:01	66	21/4/2017 22:16	64	27/3/2017 22:56	63
27/3/2017 32:31	66	1/4/2017 26:31	66	7/4/2017 33:01	66	13/4/2017 27:31	66	21/4/2017 22:21	65	27/3/2017 23:01	65
27/3/2017 33:01	66	1/4/2017 27:01	66	7/4/2017 33:31	66	13/4/2017 28:01	66	21/4/2017 22:26	63	27/3/2017 23:06	66
27/3/2017 33:31	66	1/4/2017 27:31	66	7/4/2017 34:01	66	13/4/2017 28:31	66	21/4/2017 22:31	63	27/3/2017 23:11	65
27/3/2017 34:01	66	1/4/2017 28:01	66	7/4/2017 34:31	66	13/4/2017 29:01	66	21/4/2017 22:36	64	27/3/2017 23:16	65
27/3/2017 34:31	66	1/4/2017 28:31	66	7/4/2017 35:01	66	13/4/2017 29:31	66	21/4/2017 22:41	64	27/3/2017 23:21	65
27/3/2017 35:01	66	1/4/2017 29:01	66	7/4/2017 35:31	66	13/4/2017 30:01	66	21/4/2017 22:46	64	27/3/2017 23:26	64
27/3/2017 35:31	66	1/4/2017 29:31	66	7/4/2017 36:01	66	13/4/2017 30:31	66	21/4/2017 22:51	63	27/3/2017 23:31	64
27/3/2017 36:01	66	1/4/2017 30:01	66	7/4/2017 36:31	66	13/4/2017 31:01	66	21/4/2017 22:56	63	27/3/2017 23:36	64
27/3/2017 36:31	66	1/4/2017 30:31	66	7/4/2017 37:01	66	13/4/2017 31:31	66	21/4/2017 23:01	66	27/3/2017 23:41	64
27/3/2017 37:01	66	1/4/2017 31:01	66	7/4/2017 37:31	66	13/4/2017 32:01	66	21/4/2017 23:06	64	27/3/2017 23:46	64
27/3/2017 37:31	66	1/4/2017 31:31	66	7/4/2017 38:01	66	13/4/2017 32:31	66	21/4/2017 23:11	64	27/3/2017 23:51	64
27/3/2017 38:01	66	1/4/2017 32:01	66	7/4/2017 38:31	66	13/4/2017 33:01	66	21/4/2017 23:16	64	27/3/2017 23:56	64
27/3/2017 38:31	66	1/4/2017 32:31	66	7/4/2017 39:01	66	13/4/2017 33:31	66	21/4/2017 23:21	64	27/3/2017 24:01	64
27/3/2017 39:01	66	1/4/2017 33:01	66	7/4/2017 39:31	66	13/4/2017 34:01	66	21/4/2017 23:26	64	27/3/2017 24:06	64
27/3/2017 39:31	66	1/4/2017 33:31	66	7/4/2017 40:01	66	13/4/2017 34:31	66	21/4/2017 23:31	64	27/3/2017 24:11	64
27/3/2017 40:01	66	1/4/2017 34:01	66	7/4/2017 40:31	66	13/4/2017 35:01	66	21/4/2017 23:36	64	27/3/2017 24:16	64
27/3/2017 40:31	66	1/4/2017 34:31	66	7/4/2017 41:01	66	13/4/2017 35:31	66	21/4/2017 23:41	64	27/3/2017 24:21	64
27/3/2017 41:01	66	1/4/2017 35:01	66	7/4/2017 41:31	66	13/4/2017 36:01	66	21/4/2017 23:46	64	27/3/2017 24:26	64
27/3/2017 41:31	66	1/4/2017 35:31	66	7/4/2017 42:01	66	13/4/2017 36:31	66	21/4/2017 23:51	63	27/3/2017 24:31	63
27/3/2017 42:01	66	1/4/2017 36:01	66	7/4/2017 42:31	66	13/4/2017 37:01	66	21/4/2017 23:56	63	27/3/2017 24:36	63
27/3/2017 42:31	66	1/4/2017 36:31	66	7/4/2017 43:01	66	13/4/2017 37:31	66	21/4/2017 24:01	63	27/3/2017 24:41	63
27/3/2017 43:01	66	1/4/2017 37:01	66	7/4/2017 43:31	66	13					

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
28/3/2017 22:56	63	31/3/2017 20:01	65	2/4/2017 9:06	63	2/4/2017 18:11	65	4/4/2017 7:16	62	4/4/2017 16:21	64
29/3/2017 19:01	64	31/3/2017 20:06	65	2/4/2017 9:11	64	2/4/2017 18:16	64	4/4/2017 7:21	62	4/4/2017 16:26	64
29/3/2017 19:06	65	31/3/2017 20:11	65	2/4/2017 9:16	65	2/4/2017 18:21	65	4/4/2017 7:26	62	4/4/2017 16:31	64
29/3/2017 19:11	66	31/3/2017 20:16	66	2/4/2017 9:21	64	2/4/2017 18:26	64	4/4/2017 7:31	61	4/4/2017 16:36	63
29/3/2017 19:16	65	31/3/2017 20:21	66	2/4/2017 9:26	64	2/4/2017 18:31	64	4/4/2017 7:36	62	4/4/2017 16:41	64
29/3/2017 19:21	65	31/3/2017 20:26	64	2/4/2017 9:31	64	2/4/2017 18:36	64	4/4/2017 7:41	62	4/4/2017 16:46	64
29/3/2017 19:26	65	31/3/2017 20:31	64	2/4/2017 9:36	64	2/4/2017 18:41	65	4/4/2017 7:46	63	4/4/2017 16:51	64
29/3/2017 19:31	64	31/3/2017 20:36	65	2/4/2017 9:41	64	2/4/2017 18:46	64	4/4/2017 7:51	64	4/4/2017 16:56	64
29/3/2017 19:36	63	31/3/2017 20:41	65	2/4/2017 9:46	65	2/4/2017 18:51	64	4/4/2017 7:56	63	4/4/2017 17:01	65
29/3/2017 19:41	64	31/3/2017 20:46	66	2/4/2017 9:51	65	2/4/2017 18:56	64	4/4/2017 8:01	63	4/4/2017 17:06	64
29/3/2017 19:46	64	31/3/2017 20:51	65	2/4/2017 9:56	64	2/4/2017 19:01	64	4/4/2017 8:06	62	4/4/2017 17:11	63
29/3/2017 19:51	64	31/3/2017 20:56	65	2/4/2017 10:01	64	2/4/2017 19:06	63	4/4/2017 8:11	63	4/4/2017 17:16	64
29/3/2017 19:56	64	31/3/2017 21:01	65	2/4/2017 10:06	64	2/4/2017 19:11	63	4/4/2017 8:16	63	4/4/2017 17:21	64
29/3/2017 20:01	64	31/3/2017 21:06	65	2/4/2017 10:11	64	2/4/2017 19:16	64	4/4/2017 8:21	63	4/4/2017 17:26	63
29/3/2017 20:06	63	31/3/2017 21:11	64	2/4/2017 10:16	64	2/4/2017 19:21	63	4/4/2017 8:26	63	4/4/2017 17:31	64
29/3/2017 20:11	64	31/3/2017 21:16	65	2/4/2017 10:21	64	2/4/2017 19:26	64	4/4/2017 8:31	63	4/4/2017 17:36	64
29/3/2017 20:16	65	31/3/2017 21:21	65	2/4/2017 10:26	64	2/4/2017 19:31	63	4/4/2017 8:36	64	4/4/2017 17:41	64
29/3/2017 20:21	63	31/3/2017 21:26	66	2/4/2017 10:31	65	2/4/2017 19:36	63	4/4/2017 8:41	64	4/4/2017 17:46	64
29/3/2017 20:26	64	31/3/2017 21:31	65	2/4/2017 10:36	64	2/4/2017 19:41	64	4/4/2017 8:46	63	4/4/2017 17:51	64
29/3/2017 20:31	64	31/3/2017 21:36	64	2/4/2017 10:41	63	2/4/2017 19:46	63	4/4/2017 8:51	64	4/4/2017 17:56	64
29/3/2017 20:36	63	31/3/2017 21:41	65	2/4/2017 10:46	63	2/4/2017 19:51	63	4/4/2017 8:56	64	4/4/2017 18:01	64
29/3/2017 20:41	63	31/3/2017 21:46	66	2/4/2017 10:51	63	2/4/2017 19:56	63	4/4/2017 9:01	63	4/4/2017 18:06	64
29/3/2017 20:46	64	31/3/2017 21:51	65	2/4/2017 10:56	64	2/4/2017 20:01	62	4/4/2017 9:06	65	4/4/2017 18:11	64
29/3/2017 20:51	63	31/3/2017 21:56	65	2/4/2017 11:01	65	2/4/2017 20:06	63	4/4/2017 9:11	64	4/4/2017 18:16	64
29/3/2017 20:56	63	31/3/2017 22:01	67	2/4/2017 11:06	63	2/4/2017 20:11	63	4/4/2017 9:16	63	4/4/2017 18:21	63
29/3/2017 21:01	63	31/3/2017 22:06	65	2/4/2017 11:11	64	2/4/2017 20:16	63	4/4/2017 9:21	63	4/4/2017 18:26	65
29/3/2017 21:06	64	31/3/2017 22:11	66	2/4/2017 11:16	65	2/4/2017 20:21	64	4/4/2017 9:26	63	4/4/2017 18:31	64
29/3/2017 21:11	64	31/3/2017 22:16	65	2/4/2017 11:21	63	2/4/2017 20:26	62	4/4/2017 9:31	63	4/4/2017 18:36	64
29/3/2017 21:16	63	31/3/2017 22:21	65	2/4/2017 11:26	63	2/4/2017 20:31	63	4/4/2017 9:36	64	4/4/2017 18:41	63
29/3/2017 21:21	64	31/3/2017 22:26	67	2/4/2017 11:31	63	2/4/2017 20:36	64	4/4/2017 9:41	65	4/4/2017 18:46	64
29/3/2017 21:26	63	31/3/2017 22:31	66	2/4/2017 11:36	63	2/4/2017 20:41	63	4/4/2017 9:46	64	4/4/2017 18:51	64
29/3/2017 21:31	63	31/3/2017 22:36	65	2/4/2017 11:41	66	2/4/2017 20:46	62	4/4/2017 9:51	64	4/4/2017 18:56	63
29/3/2017 21:36	63	31/3/2017 22:41	65	2/4/2017 11:46	64	2/4/2017 20:51	63	4/4/2017 9:56	64	4/4/2017 19:01	63
29/3/2017 21:41	63	31/3/2017 22:46	65	2/4/2017 11:51	64	2/4/2017 20:56	63	4/4/2017 10:01	64	4/4/2017 19:06	63
29/3/2017 21:46	63	31/3/2017 22:51	66	2/4/2017 11:56	63	2/4/2017 21:01	63	4/4/2017 10:06	65	4/4/2017 19:11	64
29/3/2017 21:51	63	31/3/2017 22:56	65	2/4/2017 12:01	63	2/4/2017 21:06	63	4/4/2017 10:11	63	4/4/2017 19:16	63
29/3/2017 21:56	63	1/4/2017 19:01	63	2/4/2017 12:06	63	2/4/2017 21:11	63	4/4/2017 10:16	63	4/4/2017 19:21	63
29/3/2017 22:01	63	1/4/2017 19:06	62	2/4/2017 12:11	63	2/4/2017 21:16	63	4/4/2017 10:21	63	4/4/2017 19:26	63
29/3/2017 22:06	63	1/4/2017 19:11	62	2/4/2017 12:16	64	2/4/2017 21:21	64	4/4/2017 10:26	64	4/4/2017 19:31	64
29/3/2017 22:11	63	1/4/2017 19:16	63	2/4/2017 12:21	64	2/4/2017 21:26	64	4/4/2017 10:31	64	4/4/2017 19:36	64
29/3/2017 22:16	64	1/4/2017 19:21	64	2/4/2017 12:26	65	2/4/2017 21:31	63	4/4/2017 10:36	64	4/4/2017 19:41	63
29/3/2017 22:21	63	1/4/2017 19:26	64	2/4/2017 12:31	64	2/4/2017 21:36	63	4/4/2017 10:41	64	4/4/2017 19:46	64
29/3/2017 22:26	63	1/4/2017 19:31	64	2/4/2017 12:36	64	2/4/2017 21:41	63	4/4/2017 10:46	63	4/4/2017 19:51	62
29/3/2017 22:31	64	1/4/2017 19:36	65	2/4/2017 12:41	65	2/4/2017 21:46	64	4/4/2017 10:51	65	4/4/2017 19:56	63
29/3/2017 22:36	63	1/4/2017 19:41	64	2/4/2017 12:46	65	2/4/2017 21:51	63	4/4/2017 10:56	63	4/4/2017 20:01	63
29/3/2017 22:41	63	1/4/2017 19:46	64	2/4/2017 12:51	64	2/4/2017 21:56	63	4/4/2017 11:01	64	4/4/2017 20:06	63
29/3/2017 22:46	64	1/4/2017 19:51	65	2/4/2017 12:56	64	2/4/2017 22:01	63	4/4/2017 11:06	62	4/4/2017 20:11	63
29/3/2017 22:51	63	1/4/2017 19:56	63	2/4/2017 13:01	64	2/4/2017 22:06	63	4/4/2017 11:11	63	4/4/2017 20:16	63
29/3/2017 22:56	63	1/4/2017 20:01	63	2/4/2017 13:06	63	2/4/2017 22:11	63	4/4/2017 11:16	63	4/4/2017 20:21	62
30/3/2017 19:01	66	1/4/2017 20:06	63	2/4/2017 13:11	63	2/4/2017 22:16	64	4/4/2017 11:21	63	4/4/2017 20:26	62
30/3/2017 19:06	66	1/4/2017 20:11	63	2/4/2017 13:16	64	2/4/2017 22:21	62	4/4/2017 11:26	64	4/4/2017 20:31	63
30/3/2017 19:11	66	1/4/2017 20:16	63	2/4/2017 13:21	64	2/4/2017 22:26	63	4/4/2017 11:31	63	4/4/2017 20:36	63
30/3/2017 19:16	66	1/4/2017 20:21	63	2/4/2017 13:26	63	2/4/2017 22:31	62	4/4/2017 11:36	63	4/4/2017 20:41	62
30/3/2017 19:21	66	1/4/2017 20:26	63	2/4/2017 13:31	64	2/4/2017 22:36	62	4/4/2017 11:41	63	4/4/2017 20:46	63
30/3/2017 19:26	66	1/4/2017 20:31	64	2/4/2017 13:36	63	2/4/2017 22:41	63	4/4/2017 11:46	63	4/4/2017 20:51	63
30/3/2017 19:31	64	1/4/2017 20:36	63	2/4/2017 13:41	63	2/4/2017 22:46	62	4/4/2017 11:51	63	4/4/2017 20:56	63
30/3/2017 19:36	64	1/4/2017 20:41	64	2/4/2017 13:46	63	2/4/2017 22:51	63	4/4/2017 11:56	63	4/4/2017 21:01	63
30/3/2017 19:41	64	1/4/2017 20:46	63	2/4/2017 13:51	63	2/4/2017 22:56	62	4/4/2017 12:01	64	4/4/2017 21:06	63
30/3/2017 19:46	65	1/4/2017 20:51	63	2/4/2017 13:56	64	3/4/2017 19:01	66	4/4/2017 12:06	64	4/4/2017 21:11	63
30/3/2017 19:51	63	1/4/2017 20:56	64	2/4/2017 14:01	63	3/4/2017 19:06	66	4/4/2017 12:11	64	4/4/2017 21:16	63
30/3/2017 19:56	64	1/4/2017 21:01	63	2/4/2017 14:06	64	3/4/2017 19:11	66	4/4/2017 12:16	66	4/4/2017 21:21	64
30/3/2017 20:01	64	1/4/2017 21:06	63	2/4/2017 14:11	64	3/4/2017 19:16	67	4/4/2017 12:21	63	4/4/2017 21:26	62
30/3/2017 20:06	63	1/4/2017 21:11	63	2/4/2017 14:16	64	3/4/2017 19:21	66	4/4/2017 12:26	64	4/4/2017 21:31	63
30/3/2017 20:11	64	1/4/2017 21:16	63	2/4/2017 14:21	64	3/4/2017 19:26	66	4/4/2017 12:31	63	4/4/2017 21:36	63
30/3/2017 20:16	64	1/4/2017 21:21	64	2/4/2017 14:26	63	3/4/2017 19:31	65	4/4/2017 12:36	64	4/4/2017 21:41	64
30/3/2017 20:21	63	1/4/2017 21:26	63	2/4/2017 14:31	63	3/4/2017 19:36	64	4/4/2017 12:41	64	4/4/2017 21:46	63
30/3/2017 20:26	63	1/4/2017 21:31	63	2/4/2017 14:36	64	3/4/2017 19:41	64	4/4/2017 12:46	64	4/4/2017 21:51	64
30/3/2017 20:31	63	1/4/2017 21:36	63	2/4/2017 14:41	64	3/4/2017 19:46	64	4/4/2017 12:51	65	4/4/2017 21:56	62
30/3/2017 20:36	63	1/4/2017 21:41	64	2/4/2017 14:46	63	3/4/2017 19:51	64	4/4/2017 12:56	64	4/4/2017 22:01	63
30/3/2017 20:41	64	1/4/2017 21:46	64	2/4/2017 14:51	63	3/4/2017 19:56	64	4/4/2017 13:01	64	4/4/2017 22:06	62
30/3/2017 20:46	64	1/4/2017 21:51	63	2/4/2017 14:56	64	3/4/2017 20:01	64	4/4/2017 13:06	63	4/4/2017 22:11	63
30/3/2017 20:51	63	1/4/2017 21:56	64	2/4/2017 15:01	64	3/4/2017 20:06	64	4/4/2017 13:11	64	4/4/2017 22:16	63
30/3/2017 20:56	63	1/4/2017 22:01	64	2/4/2017 15:06	64	3/4/2017 20:11	65	4/4/2017 13:16	64	4/4/2017 22:21	62
30/3/2017 21:01	63	1/4/2017 22:06	63	2/4/2017 15:11	64	3/4/2017 20:16	64	4/4/2017 13:21	64	4/4/2017 22:26	61
30/3/2017 21:06	63	1/4/2017 22:11	63	2/4/2017 15:16	64	3/4/2017 20:21	64	4/4/2017 13:26	64	4/4/2017 22:31	62
30/3/2017 21:11	64	1/4/2017 22:16	63	2/4/2017 15:21	64						

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
5/4/2017 21:26	63	7/4/2017 22:31	63	9/4/2017 11:36	63	9/4/2017 20:41	64	11/4/2017 21:46	63	13/4/2017 22:51	64
5/4/2017 21:31	63	7/4/2017 22:36	64	9/4/2017 11:41	64	9/4/2017 20:46	63	11/4/2017 21:51	63	13/4/2017 22:56	63
5/4/2017 21:36	63	7/4/2017 22:41	63	9/4/2017 11:46	63	9/4/2017 20:51	62	11/4/2017 21:56	63	14/4/2017 7:01	62
5/4/2017 21:41	64	7/4/2017 22:46	63	9/4/2017 11:51	62	9/4/2017 20:56	62	11/4/2017 22:01	64	14/4/2017 7:06	62
5/4/2017 21:46	63	7/4/2017 22:51	63	9/4/2017 11:56	64	9/4/2017 21:01	63	11/4/2017 22:06	64	14/4/2017 7:11	62
5/4/2017 21:51	65	7/4/2017 22:56	62	9/4/2017 12:01	62	9/4/2017 21:06	62	11/4/2017 22:11	64	14/4/2017 7:16	62
5/4/2017 21:56	63	8/4/2017 19:01	63	9/4/2017 12:06	63	9/4/2017 21:11	62	11/4/2017 22:16	64	14/4/2017 7:21	63
5/4/2017 22:01	62	8/4/2017 19:06	64	9/4/2017 12:11	63	9/4/2017 21:16	62	11/4/2017 22:21	64	14/4/2017 7:26	62
5/4/2017 22:06	63	8/4/2017 19:11	64	9/4/2017 12:16	64	9/4/2017 21:21	62	11/4/2017 22:26	64	14/4/2017 7:31	62
5/4/2017 22:11	63	8/4/2017 19:16	64	9/4/2017 12:21	63	9/4/2017 21:26	63	11/4/2017 22:31	64	14/4/2017 7:36	63
5/4/2017 22:16	63	8/4/2017 19:21	63	9/4/2017 12:26	64	9/4/2017 21:31	62	11/4/2017 22:36	63	14/4/2017 7:41	63
5/4/2017 22:21	63	8/4/2017 19:26	64	9/4/2017 12:31	64	9/4/2017 21:36	62	11/4/2017 22:41	64	14/4/2017 7:46	63
5/4/2017 22:26	63	8/4/2017 19:31	65	9/4/2017 12:36	64	9/4/2017 21:41	62	11/4/2017 22:46	64	14/4/2017 7:51	63
5/4/2017 22:31	63	8/4/2017 19:36	64	9/4/2017 12:41	64	9/4/2017 21:46	63	11/4/2017 22:51	64	14/4/2017 7:56	63
5/4/2017 22:36	64	8/4/2017 19:41	64	9/4/2017 12:46	64	9/4/2017 21:51	62	11/4/2017 22:56	64	14/4/2017 8:01	63
5/4/2017 22:41	63	8/4/2017 19:46	63	9/4/2017 12:51	64	9/4/2017 21:56	62	12/4/2017 19:01	67	14/4/2017 8:06	64
5/4/2017 22:46	62	8/4/2017 19:51	63	9/4/2017 12:56	64	9/4/2017 22:01	62	12/4/2017 19:06	68	14/4/2017 8:11	64
5/4/2017 22:51	62	8/4/2017 19:56	63	9/4/2017 13:01	64	9/4/2017 22:06	63	12/4/2017 19:11	67	14/4/2017 8:16	63
5/4/2017 22:56	63	8/4/2017 20:01	63	9/4/2017 13:06	65	9/4/2017 22:11	62	12/4/2017 19:16	67	14/4/2017 8:21	63
6/4/2017 19:01	65	8/4/2017 20:06	62	9/4/2017 13:11	64	9/4/2017 22:16	62	12/4/2017 19:21	67	14/4/2017 8:26	65
6/4/2017 19:06	65	8/4/2017 20:11	63	9/4/2017 13:16	64	9/4/2017 22:21	62	12/4/2017 19:26	65	14/4/2017 8:31	64
6/4/2017 19:11	65	8/4/2017 20:16	63	9/4/2017 13:21	66	9/4/2017 22:26	61	12/4/2017 19:31	65	14/4/2017 8:36	64
6/4/2017 19:16	65	8/4/2017 20:21	62	9/4/2017 13:26	64	9/4/2017 22:31	62	12/4/2017 19:36	65	14/4/2017 8:41	64
6/4/2017 19:21	65	8/4/2017 20:26	63	9/4/2017 13:31	64	9/4/2017 22:36	62	12/4/2017 19:41	65	14/4/2017 8:46	64
6/4/2017 19:26	66	8/4/2017 20:31	63	9/4/2017 13:36	63	9/4/2017 22:41	62	12/4/2017 19:46	65	14/4/2017 8:51	64
6/4/2017 19:31	64	8/4/2017 20:36	62	9/4/2017 13:41	64	9/4/2017 22:46	62	12/4/2017 19:51	66	14/4/2017 8:56	64
6/4/2017 19:36	64	8/4/2017 20:41	64	9/4/2017 13:46	63	9/4/2017 22:51	63	12/4/2017 19:56	65	14/4/2017 9:01	65
6/4/2017 19:41	64	8/4/2017 20:46	63	9/4/2017 13:51	64	9/4/2017 22:56	62	12/4/2017 20:01	65	14/4/2017 9:06	64
6/4/2017 19:46	64	8/4/2017 20:51	61	9/4/2017 13:56	63	10/4/2017 19:01	66	12/4/2017 20:06	66	14/4/2017 9:11	64
6/4/2017 19:51	63	8/4/2017 20:56	63	9/4/2017 14:01	63	10/4/2017 19:06	66	12/4/2017 20:11	65	14/4/2017 9:16	63
6/4/2017 19:56	64	8/4/2017 21:01	63	9/4/2017 14:06	63	10/4/2017 19:11	66	12/4/2017 20:16	65	14/4/2017 9:21	64
6/4/2017 20:01	64	8/4/2017 21:06	63	9/4/2017 14:11	63	10/4/2017 19:16	66	12/4/2017 20:21	65	14/4/2017 9:26	64
6/4/2017 20:06	63	8/4/2017 21:11	64	9/4/2017 14:16	63	10/4/2017 19:21	66	12/4/2017 20:26	65	14/4/2017 9:31	65
6/4/2017 20:11	63	8/4/2017 21:16	63	9/4/2017 14:21	63	10/4/2017 19:26	64	12/4/2017 20:31	66	14/4/2017 9:36	64
6/4/2017 20:16	64	8/4/2017 21:21	63	9/4/2017 14:26	63	10/4/2017 19:31	64	12/4/2017 20:36	64	14/4/2017 9:41	65
6/4/2017 20:21	63	8/4/2017 21:26	63	9/4/2017 14:31	63	10/4/2017 19:36	64	12/4/2017 20:41	65	14/4/2017 9:46	65
6/4/2017 20:26	63	8/4/2017 21:31	63	9/4/2017 14:36	63	10/4/2017 19:41	64	12/4/2017 20:46	65	14/4/2017 9:51	64
6/4/2017 20:31	63	8/4/2017 21:36	63	9/4/2017 14:41	64	10/4/2017 19:46	64	12/4/2017 20:51	65	14/4/2017 9:56	65
6/4/2017 20:36	63	8/4/2017 21:41	63	9/4/2017 14:46	64	10/4/2017 19:51	64	12/4/2017 20:56	64	14/4/2017 10:01	64
6/4/2017 20:41	62	8/4/2017 21:46	62	9/4/2017 14:51	63	10/4/2017 19:56	64	12/4/2017 21:01	64	14/4/2017 10:06	64
6/4/2017 20:46	62	8/4/2017 21:51	63	9/4/2017 14:56	64	10/4/2017 20:01	64	12/4/2017 21:06	64	14/4/2017 10:11	64
6/4/2017 20:51	62	8/4/2017 21:56	63	9/4/2017 15:01	63	10/4/2017 20:06	64	12/4/2017 21:11	64	14/4/2017 10:16	63
6/4/2017 20:56	62	8/4/2017 22:01	63	9/4/2017 15:06	63	10/4/2017 20:11	63	12/4/2017 21:16	65	14/4/2017 10:21	64
6/4/2017 21:01	63	8/4/2017 22:06	63	9/4/2017 15:11	64	10/4/2017 20:16	64	12/4/2017 21:21	64	14/4/2017 10:26	64
6/4/2017 21:06	63	8/4/2017 22:11	63	9/4/2017 15:16	63	10/4/2017 20:21	63	12/4/2017 21:26	63	14/4/2017 10:31	64
6/4/2017 21:11	62	8/4/2017 22:16	63	9/4/2017 15:21	63	10/4/2017 20:26	63	12/4/2017 21:31	64	14/4/2017 10:36	64
6/4/2017 21:16	63	8/4/2017 22:21	63	9/4/2017 15:26	64	10/4/2017 20:31	63	12/4/2017 21:36	64	14/4/2017 10:41	64
6/4/2017 21:21	63	8/4/2017 22:26	63	9/4/2017 15:31	64	10/4/2017 20:36	64	12/4/2017 21:41	64	14/4/2017 10:46	64
6/4/2017 21:26	62	8/4/2017 22:31	64	9/4/2017 15:36	65	10/4/2017 20:41	64	12/4/2017 21:46	64	14/4/2017 10:51	65
6/4/2017 21:31	63	8/4/2017 22:36	63	9/4/2017 15:41	67	10/4/2017 20:46	63	12/4/2017 21:51	64	14/4/2017 10:56	63
6/4/2017 21:36	64	8/4/2017 22:41	63	9/4/2017 15:46	67	10/4/2017 20:51	63	12/4/2017 21:56	64	14/4/2017 11:01	65
6/4/2017 21:41	62	8/4/2017 22:46	65	9/4/2017 15:51	67	10/4/2017 20:56	63	12/4/2017 22:01	65	14/4/2017 11:06	65
6/4/2017 21:46	64	8/4/2017 22:51	63	9/4/2017 15:56	68	10/4/2017 21:01	63	12/4/2017 22:06	65	14/4/2017 11:11	64
6/4/2017 21:51	63	8/4/2017 22:56	63	9/4/2017 16:01	67	10/4/2017 21:06	63	12/4/2017 22:11	64	14/4/2017 11:16	64
6/4/2017 21:56	63	9/4/2017 7:01	63	9/4/2017 16:06	69	10/4/2017 21:11	63	12/4/2017 22:16	64	14/4/2017 11:21	64
6/4/2017 22:01	63	9/4/2017 7:06	61	9/4/2017 16:11	66	10/4/2017 21:16	63	12/4/2017 22:21	64	14/4/2017 11:26	64
6/4/2017 22:06	63	9/4/2017 7:11	62	9/4/2017 16:16	65	10/4/2017 21:21	63	12/4/2017 22:26	63	14/4/2017 11:31	63
6/4/2017 22:11	63	9/4/2017 7:16	67	9/4/2017 16:21	66	10/4/2017 21:26	62	12/4/2017 22:31	64	14/4/2017 11:36	62
6/4/2017 22:16	63	9/4/2017 7:21	62	9/4/2017 16:26	67	10/4/2017 21:31	63	12/4/2017 22:36	64	14/4/2017 11:41	63
6/4/2017 22:21	63	9/4/2017 7:26	61	9/4/2017 16:31	69	10/4/2017 21:36	62	12/4/2017 22:41	63	14/4/2017 11:46	62
6/4/2017 22:26	62	9/4/2017 7:31	62	9/4/2017 16:36	67	10/4/2017 21:41	63	12/4/2017 22:46	65	14/4/2017 11:51	63
6/4/2017 22:31	63	9/4/2017 7:36	63	9/4/2017 16:41	68	10/4/2017 21:46	63	12/4/2017 22:51	64	14/4/2017 11:56	62
6/4/2017 22:36	63	9/4/2017 7:41	63	9/4/2017 16:46	65	10/4/2017 21:51	63	12/4/2017 22:56	63	14/4/2017 12:01	62
6/4/2017 22:41	63	9/4/2017 7:46	62	9/4/2017 16:51	65	10/4/2017 21:56	62	13/4/2017 19:01	65	14/4/2017 12:06	63
6/4/2017 22:46	62	9/4/2017 7:51	62	9/4/2017 16:56	64	10/4/2017 22:01	62	13/4/2017 19:06	65	14/4/2017 12:11	63
6/4/2017 22:51	63	9/4/2017 7:56	63	9/4/2017 17:01	64	10/4/2017 22:06	63	13/4/2017 19:11	66	14/4/2017 12:16	64
6/4/2017 22:56	62	9/4/2017 8:01	62	9/4/2017 17:06	64	10/4/2017 22:11	63	13/4/2017 19:16	66	14/4/2017 12:21	64
7/4/2017 19:01	65	9/4/2017 8:06	63	9/4/2017 17:11	65	10/4/2017 22:16	63	13/4/2017 19:21	65	14/4/2017 12:26	64
7/4/2017 19:06	66	9/4/2017 8:11	64	9/4/2017 17:16	65	10/4/2017 22:21	63	13/4/2017 19:26	65	14/4/2017 12:31	64
7/4/2017 19:11	66	9/4/2017 8:16	63	9/4/2017 17:21	64	10/4/2017 22:26	63	13/4/2017 19:31	64	14/4/2017 12:36	64
7/4/2017 19:16	65	9/4/2017 8:21	63	9/4/2017 17:26	65	10/4/2017 22:31	63	13/4/2017 19:36	64	14/4/2017 12:41	64
7/4/2017 19:21	66	9/4/2017 8:26	63	9/4/2017 17:31	66	10/4/2017 22:36	63	13/4/2017 19:41	66	14/4/2017 12:46	64
7/4/2017 19:26	63	9/4/2017 8:31	64	9/4/2017 17:36	66	10/4/2017 22:41	62	13/4/2017 19:46	64	14/4/2017 12:51	64
7/4/2017 19:31	62	9/4/2017 8:36	63	9/4/2017 17:41	59	10/4/2017 22:46	62	13/4/2017 19:51	64	14/4/2017 12:56	64
7/4/2017 19:36	63	9/4/2017 8:41	64	9/4/2017 17:46	67	10/4/2017 22:51	62	13/4/2017 19:56	64	14/4/2017 13:01	65
7/4/2											

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
14/4/2017 15:56	65	15/4/2017 9:01	63	15/4/2017 18:06	64	16/4/2017 11:11	64	16/4/2017 20:16	63	17/4/2017 13:21	63
14/4/2017 16:01	64	15/4/2017 9:06	64	15/4/2017 18:11	64	16/4/2017 11:16	65	16/4/2017 20:21	63	17/4/2017 13:26	64
14/4/2017 16:06	63	15/4/2017 9:11	64	15/4/2017 18:16	64	16/4/2017 11:21	64	16/4/2017 20:26	63	17/4/2017 13:31	64
14/4/2017 16:11	64	15/4/2017 9:16	63	15/4/2017 18:21	64	16/4/2017 11:26	64	16/4/2017 20:31	62	17/4/2017 13:36	63
14/4/2017 16:16	65	15/4/2017 9:21	63	15/4/2017 18:26	63	16/4/2017 11:31	63	16/4/2017 20:36	62	17/4/2017 13:41	64
14/4/2017 16:21	64	15/4/2017 9:26	63	15/4/2017 18:31	63	16/4/2017 11:36	64	16/4/2017 20:41	63	17/4/2017 13:46	64
14/4/2017 16:26	64	15/4/2017 9:31	64	15/4/2017 18:36	64	16/4/2017 11:41	66	16/4/2017 20:46	63	17/4/2017 13:51	64
14/4/2017 16:31	63	15/4/2017 9:36	65	15/4/2017 18:41	63	16/4/2017 11:46	63	16/4/2017 20:51	62	17/4/2017 13:56	64
14/4/2017 16:36	64	15/4/2017 9:41	64	15/4/2017 18:46	63	16/4/2017 11:51	63	16/4/2017 20:56	62	17/4/2017 14:01	64
14/4/2017 16:41	64	15/4/2017 9:46	64	15/4/2017 18:51	64	16/4/2017 11:56	63	16/4/2017 21:01	63	17/4/2017 14:06	63
14/4/2017 16:46	63	15/4/2017 9:51	64	15/4/2017 18:56	63	16/4/2017 12:01	63	16/4/2017 21:06	63	17/4/2017 14:11	64
14/4/2017 16:51	63	15/4/2017 9:56	64	15/4/2017 19:01	63	16/4/2017 12:06	63	16/4/2017 21:11	62	17/4/2017 14:16	63
14/4/2017 16:56	64	15/4/2017 10:01	64	15/4/2017 19:06	64	16/4/2017 12:11	64	16/4/2017 21:16	62	17/4/2017 14:21	63
14/4/2017 17:01	64	15/4/2017 10:06	63	15/4/2017 19:11	64	16/4/2017 12:16	64	16/4/2017 21:21	63	17/4/2017 14:26	64
14/4/2017 17:06	63	15/4/2017 10:11	64	15/4/2017 19:16	63	16/4/2017 12:21	65	16/4/2017 21:26	62	17/4/2017 14:31	64
14/4/2017 17:11	63	15/4/2017 10:16	64	15/4/2017 19:21	64	16/4/2017 12:26	64	16/4/2017 21:31	63	17/4/2017 14:36	63
14/4/2017 17:16	63	15/4/2017 10:21	64	15/4/2017 19:26	63	16/4/2017 12:31	64	16/4/2017 21:36	62	17/4/2017 14:41	64
14/4/2017 17:21	64	15/4/2017 10:26	64	15/4/2017 19:31	63	16/4/2017 12:36	64	16/4/2017 21:41	63	17/4/2017 14:46	63
14/4/2017 17:26	64	15/4/2017 10:31	64	15/4/2017 19:36	63	16/4/2017 12:41	65	16/4/2017 21:46	63	17/4/2017 14:51	64
14/4/2017 17:31	64	15/4/2017 10:36	64	15/4/2017 19:41	63	16/4/2017 12:46	65	16/4/2017 21:51	62	17/4/2017 14:56	63
14/4/2017 17:36	63	15/4/2017 10:41	64	15/4/2017 19:46	65	16/4/2017 12:51	65	16/4/2017 21:56	62	17/4/2017 15:01	64
14/4/2017 17:41	63	15/4/2017 10:46	64	15/4/2017 19:51	63	16/4/2017 12:56	64	16/4/2017 22:01	63	17/4/2017 15:06	63
14/4/2017 17:46	63	15/4/2017 10:51	63	15/4/2017 19:56	63	16/4/2017 13:01	64	16/4/2017 22:06	63	17/4/2017 15:11	63
14/4/2017 17:51	63	15/4/2017 10:56	64	15/4/2017 20:01	63	16/4/2017 13:06	64	16/4/2017 22:11	63	17/4/2017 15:16	63
14/4/2017 17:56	64	15/4/2017 11:01	63	15/4/2017 20:06	63	16/4/2017 13:11	63	16/4/2017 22:16	63	17/4/2017 15:21	64
14/4/2017 18:01	64	15/4/2017 11:06	64	15/4/2017 20:11	63	16/4/2017 13:16	64	16/4/2017 22:21	63	17/4/2017 15:26	63
14/4/2017 18:06	63	15/4/2017 11:11	64	15/4/2017 20:16	64	16/4/2017 13:21	64	16/4/2017 22:26	63	17/4/2017 15:31	63
14/4/2017 18:11	63	15/4/2017 11:16	64	15/4/2017 20:21	62	16/4/2017 13:26	63	16/4/2017 22:31	63	17/4/2017 15:36	63
14/4/2017 18:16	63	15/4/2017 11:21	64	15/4/2017 20:26	62	16/4/2017 13:31	63	16/4/2017 22:36	62	17/4/2017 15:41	64
14/4/2017 18:21	63	15/4/2017 11:26	66	15/4/2017 20:31	63	16/4/2017 13:36	63	16/4/2017 22:41	63	17/4/2017 15:46	63
14/4/2017 18:26	64	15/4/2017 11:31	64	15/4/2017 20:36	63	16/4/2017 13:41	63	16/4/2017 22:46	62	17/4/2017 15:51	63
14/4/2017 18:31	64	15/4/2017 11:36	64	15/4/2017 20:41	62	16/4/2017 13:46	63	16/4/2017 22:51	62	17/4/2017 15:56	63
14/4/2017 18:36	64	15/4/2017 11:41	64	15/4/2017 20:46	63	16/4/2017 13:51	63	16/4/2017 22:56	62	17/4/2017 16:01	63
14/4/2017 18:41	63	15/4/2017 11:46	64	15/4/2017 20:51	62	16/4/2017 13:56	63	17/4/2017 7:01	63	17/4/2017 16:06	63
14/4/2017 18:46	63	15/4/2017 11:51	64	15/4/2017 20:56	62	16/4/2017 14:01	64	17/4/2017 7:06	61	17/4/2017 16:11	64
14/4/2017 18:51	64	15/4/2017 11:56	64	15/4/2017 21:01	63	16/4/2017 14:06	63	17/4/2017 7:11	64	17/4/2017 16:16	64
14/4/2017 18:56	63	15/4/2017 12:01	64	15/4/2017 21:06	62	16/4/2017 14:11	63	17/4/2017 7:16	61	17/4/2017 16:21	64
14/4/2017 19:01	64	15/4/2017 12:06	65	15/4/2017 21:11	62	16/4/2017 14:16	63	17/4/2017 7:21	61	17/4/2017 16:26	64
14/4/2017 19:06	63	15/4/2017 12:11	64	15/4/2017 21:16	63	16/4/2017 14:21	63	17/4/2017 7:26	61	17/4/2017 16:31	64
14/4/2017 19:11	64	15/4/2017 12:16	64	15/4/2017 21:21	64	16/4/2017 14:26	64	17/4/2017 7:31	63	17/4/2017 16:36	64
14/4/2017 19:16	63	15/4/2017 12:21	64	15/4/2017 21:26	63	16/4/2017 14:31	63	17/4/2017 7:36	62	17/4/2017 16:41	63
14/4/2017 19:21	63	15/4/2017 12:26	64	15/4/2017 21:31	62	16/4/2017 14:36	63	17/4/2017 7:41	62	17/4/2017 16:46	64
14/4/2017 19:26	63	15/4/2017 12:31	64	15/4/2017 21:36	63	16/4/2017 14:41	63	17/4/2017 7:46	63	17/4/2017 16:51	63
14/4/2017 19:31	64	15/4/2017 12:36	64	15/4/2017 21:41	63	16/4/2017 14:46	63	17/4/2017 7:51	62	17/4/2017 16:56	64
14/4/2017 19:36	64	15/4/2017 12:41	64	15/4/2017 21:46	62	16/4/2017 14:51	63	17/4/2017 7:56	61	17/4/2017 17:01	63
14/4/2017 19:41	65	15/4/2017 12:46	65	15/4/2017 21:51	63	16/4/2017 14:56	63	17/4/2017 8:01	62	17/4/2017 17:06	63
14/4/2017 19:46	64	15/4/2017 12:51	64	15/4/2017 21:56	63	16/4/2017 15:01	64	17/4/2017 8:06	63	17/4/2017 17:11	65
14/4/2017 19:51	63	15/4/2017 12:56	65	15/4/2017 22:01	63	16/4/2017 15:06	63	17/4/2017 8:11	62	17/4/2017 17:16	63
14/4/2017 19:56	62	15/4/2017 13:01	64	15/4/2017 22:06	62	16/4/2017 15:11	63	17/4/2017 8:16	63	17/4/2017 17:21	63
14/4/2017 20:01	63	15/4/2017 13:06	64	15/4/2017 22:11	64	16/4/2017 15:16	63	17/4/2017 8:21	63	17/4/2017 17:26	63
14/4/2017 20:06	62	15/4/2017 13:11	64	15/4/2017 22:16	63	16/4/2017 15:21	64	17/4/2017 8:26	62	17/4/2017 17:31	63
14/4/2017 20:11	63	15/4/2017 13:16	64	15/4/2017 22:21	62	16/4/2017 15:26	63	17/4/2017 8:31	63	17/4/2017 17:36	63
14/4/2017 20:16	62	15/4/2017 13:21	64	15/4/2017 22:26	62	16/4/2017 15:31	64	17/4/2017 8:36	65	17/4/2017 17:41	63
14/4/2017 20:21	62	15/4/2017 13:26	64	15/4/2017 22:31	64	16/4/2017 15:36	63	17/4/2017 8:41	66	17/4/2017 17:46	64
14/4/2017 20:26	63	15/4/2017 13:31	64	15/4/2017 22:36	63	16/4/2017 15:41	63	17/4/2017 8:46	63	17/4/2017 17:51	63
14/4/2017 20:31	63	15/4/2017 13:36	65	15/4/2017 22:41	63	16/4/2017 15:46	64	17/4/2017 8:51	64	17/4/2017 17:56	63
14/4/2017 20:36	63	15/4/2017 13:41	64	15/4/2017 22:46	63	16/4/2017 15:51	63	17/4/2017 8:56	63	17/4/2017 18:01	64
14/4/2017 20:41	63	15/4/2017 13:46	64	15/4/2017 22:51	62	16/4/2017 15:56	64	17/4/2017 9:01	64	17/4/2017 18:06	64
14/4/2017 20:46	63	15/4/2017 13:51	64	15/4/2017 22:56	63	16/4/2017 16:01	64	17/4/2017 9:06	63	17/4/2017 18:11	63
14/4/2017 20:51	63	15/4/2017 13:56	65	16/4/2017 7:01	69	16/4/2017 16:06	64	17/4/2017 9:11	63	17/4/2017 18:16	64
14/4/2017 20:56	64	15/4/2017 14:01	63	16/4/2017 7:06	61	16/4/2017 16:11	65	17/4/2017 9:16	63	17/4/2017 18:21	63
14/4/2017 21:01	63	15/4/2017 14:06	64	16/4/2017 7:11	60	16/4/2017 16:16	63	17/4/2017 9:21	63	17/4/2017 18:26	63
14/4/2017 21:06	63	15/4/2017 14:11	64	16/4/2017 7:16	60	16/4/2017 16:21	63	17/4/2017 9:26	63	17/4/2017 18:31	63
14/4/2017 21:11	63	15/4/2017 14:16	64	16/4/2017 7:21	61	16/4/2017 16:26	64	17/4/2017 9:31	64	17/4/2017 18:36	63
14/4/2017 21:16	62	15/4/2017 14:21	63	16/4/2017 7:26	64	16/4/2017 16:31	63	17/4/2017 9:36	63	17/4/2017 18:41	64
14/4/2017 21:21	64	15/4/2017 14:26	63	16/4/2017 7:31	62	16/4/2017 16:36	63	17/4/2017 9:41	63	17/4/2017 18:46	63
14/4/2017 21:26	63	15/4/2017 14:31	64	16/4/2017 7:36	62	16/4/2017 16:41	64	17/4/2017 9:46	63	17/4/2017 18:51	63
14/4/2017 21:31	64	15/4/2017 14:36	64	16/4/2017 7:41	62	16/4/2017 16:46	63	17/4/2017 9:51	63	17/4/2017 18:56	65
14/4/2017 21:36	65	15/4/2017 14:41	64	16/4/2017 7:46	62	16/4/2017 16:51	64	17/4/2017 9:56	63	17/4/2017 19:01	63
14/4/2017 21:41	62	15/4/2017 14:46	64	16/4/2017 7:51	62	16/4/2017 16:56	63	17/4/2017 10:01	64	17/4/2017 19:06	63
14/4/2017 21:46	63	15/4/2017 14:51	64	16/4/2017 7:56	61	16/4/2017 17:01	64	17/4/2017 10:06	63	17/4/2017 19:11	64
14/4/2017 21:51	62	15/4/2017 14:56	63	16/4/2017 8:01	62	16/4/2017 17:06	63	17/4/2017 10:11	64	17/4/2017 19:16	63
14/4/2017 21:56	64	15/4/2017 15:01	64	16/4/2017 8:06	63	16/4/2017 17:11	64	17/4/2017 10:16	64	17/4/2017 19:21	64
14/4/2017 22:01	64	15/4/2017 15:06	64	16/4/2017 8:11	62	16/4/2017 1					

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
17/4/2017 22:26	62	20/4/2017 19:31	65	22/4/2017 20:36	63	23/4/2017 13:41	63	23/4/2017 22:46	63	26/4/2017 19:51	65
17/4/2017 22:31	63	20/4/2017 19:36	64	22/4/2017 20:41	64	23/4/2017 13:46	63	23/4/2017 22:51	63	26/4/2017 19:56	65
17/4/2017 22:36	62	20/4/2017 19:41	65	22/4/2017 20:46	63	23/4/2017 13:51	64	23/4/2017 22:56	62	26/4/2017 20:01	64
17/4/2017 22:41	62	20/4/2017 19:46	64	22/4/2017 20:51	64	23/4/2017 13:56	63	24/4/2017 19:01	65	26/4/2017 20:06	65
17/4/2017 22:46	62	20/4/2017 19:51	64	22/4/2017 20:56	64	23/4/2017 14:01	63	24/4/2017 19:06	65	26/4/2017 20:11	64
17/4/2017 22:51	62	20/4/2017 19:56	64	22/4/2017 21:01	63	23/4/2017 14:06	64	24/4/2017 19:11	65	26/4/2017 20:16	65
17/4/2017 22:56	62	20/4/2017 20:01	64	22/4/2017 21:06	64	23/4/2017 14:11	64	24/4/2017 19:16	66	26/4/2017 20:21	65
18/4/2017 19:01	66	20/4/2017 20:06	64	22/4/2017 21:11	64	23/4/2017 14:16	64	24/4/2017 19:21	65	26/4/2017 20:26	64
18/4/2017 19:06	66	20/4/2017 20:11	64	22/4/2017 21:16	63	23/4/2017 14:21	64	24/4/2017 19:26	65	26/4/2017 20:31	64
18/4/2017 19:11	66	20/4/2017 20:16	64	22/4/2017 21:21	64	23/4/2017 14:26	64	24/4/2017 19:31	64	26/4/2017 20:36	65
18/4/2017 19:16	68	20/4/2017 20:21	63	22/4/2017 21:26	64	23/4/2017 14:31	65	24/4/2017 19:36	64	26/4/2017 20:41	64
18/4/2017 19:21	67	20/4/2017 20:26	64	22/4/2017 21:31	63	23/4/2017 14:36	65	24/4/2017 19:41	65	26/4/2017 20:46	64
18/4/2017 19:26	66	20/4/2017 20:31	64	22/4/2017 21:36	65	23/4/2017 14:41	64	24/4/2017 19:46	64	26/4/2017 20:51	64
18/4/2017 19:31	64	20/4/2017 20:36	63	22/4/2017 21:41	64	23/4/2017 14:46	65	24/4/2017 19:51	65	26/4/2017 20:56	64
18/4/2017 19:36	64	20/4/2017 20:41	63	22/4/2017 21:46	64	23/4/2017 14:51	64	24/4/2017 19:56	64	26/4/2017 21:01	65
18/4/2017 19:41	64	20/4/2017 20:46	64	22/4/2017 21:51	64	23/4/2017 14:56	64	24/4/2017 20:01	64	26/4/2017 21:06	64
18/4/2017 19:46	64	20/4/2017 20:51	63	22/4/2017 21:56	63	23/4/2017 15:01	64	24/4/2017 20:06	64	26/4/2017 21:11	65
18/4/2017 19:51	64	20/4/2017 20:56	63	22/4/2017 22:01	63	23/4/2017 15:06	63	24/4/2017 20:11	65	26/4/2017 21:16	65
18/4/2017 19:56	65	20/4/2017 21:01	63	22/4/2017 22:06	66	23/4/2017 15:11	64	24/4/2017 20:16	64	26/4/2017 21:21	64
18/4/2017 20:01	64	20/4/2017 21:06	63	22/4/2017 22:11	64	23/4/2017 15:16	64	24/4/2017 20:21	65	26/4/2017 21:26	64
18/4/2017 20:06	63	20/4/2017 21:11	63	22/4/2017 22:16	64	23/4/2017 15:21	64	24/4/2017 20:26	64	26/4/2017 21:31	64
18/4/2017 20:11	64	20/4/2017 21:16	63	22/4/2017 22:21	64	23/4/2017 15:26	64	24/4/2017 20:31	64	26/4/2017 21:36	64
18/4/2017 20:16	65	20/4/2017 21:21	64	22/4/2017 22:26	65	23/4/2017 15:31	65	24/4/2017 20:36	63	26/4/2017 21:41	65
18/4/2017 20:21	65	20/4/2017 21:26	63	22/4/2017 22:31	64	23/4/2017 15:36	64	24/4/2017 20:41	64	26/4/2017 21:46	64
18/4/2017 20:26	67	20/4/2017 21:31	63	22/4/2017 22:36	64	23/4/2017 15:41	64	24/4/2017 20:46	63	26/4/2017 21:51	64
18/4/2017 20:31	64	20/4/2017 21:36	63	22/4/2017 22:41	64	23/4/2017 15:46	65	24/4/2017 20:51	64	26/4/2017 21:56	64
18/4/2017 20:36	63	20/4/2017 21:41	63	22/4/2017 22:46	63	23/4/2017 15:51	64	24/4/2017 20:56	63	26/4/2017 22:01	64
18/4/2017 20:41	63	20/4/2017 21:46	63	22/4/2017 22:51	63	23/4/2017 15:56	63	24/4/2017 21:01	63	26/4/2017 22:06	64
18/4/2017 20:46	63	20/4/2017 21:51	63	22/4/2017 22:56	63	23/4/2017 16:01	64	24/4/2017 21:06	63	26/4/2017 22:11	65
18/4/2017 20:51	63	20/4/2017 21:56	63	23/4/2017 7:01	65	23/4/2017 16:06	63	24/4/2017 21:11	63	26/4/2017 22:16	64
18/4/2017 20:56	62	20/4/2017 22:01	63	23/4/2017 7:06	62	23/4/2017 16:11	64	24/4/2017 21:16	63	26/4/2017 22:21	64
18/4/2017 21:01	63	20/4/2017 22:06	63	23/4/2017 7:11	63	23/4/2017 16:16	64	24/4/2017 21:21	65	26/4/2017 22:26	63
18/4/2017 21:06	63	20/4/2017 22:11	63	23/4/2017 7:16	62	23/4/2017 16:21	65	24/4/2017 21:26	63	26/4/2017 22:31	64
18/4/2017 21:11	63	20/4/2017 22:16	63	23/4/2017 7:21	62	23/4/2017 16:26	64	24/4/2017 21:31	63	26/4/2017 22:36	64
18/4/2017 21:16	64	20/4/2017 22:21	63	23/4/2017 7:26	63	23/4/2017 16:31	66	24/4/2017 21:36	63	26/4/2017 22:41	64
18/4/2017 21:21	63	20/4/2017 22:26	64	23/4/2017 7:31	62	23/4/2017 16:36	64	24/4/2017 21:41	64	26/4/2017 22:46	63
18/4/2017 21:26	63	20/4/2017 22:31	63	23/4/2017 7:36	62	23/4/2017 16:41	65	24/4/2017 21:46	63	26/4/2017 22:51	64
18/4/2017 21:31	63	20/4/2017 22:36	63	23/4/2017 7:41	62	23/4/2017 16:46	66	24/4/2017 21:51	64	26/4/2017 22:56	62
18/4/2017 21:36	63	20/4/2017 22:41	63	23/4/2017 7:46	63	23/4/2017 16:51	65	24/4/2017 21:56	64		
18/4/2017 21:41	62	20/4/2017 22:46	63	23/4/2017 7:51	63	23/4/2017 16:56	65	24/4/2017 22:01	63	Night time: 23:00-07:00	
18/4/2017 21:46	62	20/4/2017 22:51	62	23/4/2017 7:56	63	23/4/2017 17:01	65	24/4/2017 22:06	63		
18/4/2017 21:51	63	20/4/2017 22:56	62	23/4/2017 8:01	63	23/4/2017 17:06	65	24/4/2017 22:11	63	27/3/2017 0:01	61
18/4/2017 21:56	63	21/4/2017 19:01	64	23/4/2017 8:06	63	23/4/2017 17:11	65	24/4/2017 22:16	63	27/3/2017 0:06	61
18/4/2017 22:01	62	21/4/2017 19:06	64	23/4/2017 8:11	63	23/4/2017 17:16	65	24/4/2017 22:21	63	27/3/2017 0:11	62
18/4/2017 22:06	63	21/4/2017 19:11	64	23/4/2017 8:16	63	23/4/2017 17:21	66	24/4/2017 22:26	64	27/3/2017 0:16	62
18/4/2017 22:11	62	21/4/2017 19:16	65	23/4/2017 8:21	64	23/4/2017 17:26	66	24/4/2017 22:31	63	27/3/2017 0:21	61
18/4/2017 22:16	63	21/4/2017 19:21	65	23/4/2017 8:26	64	23/4/2017 17:31	66	24/4/2017 22:36	63	27/3/2017 0:26	61
18/4/2017 22:21	63	21/4/2017 19:26	67	23/4/2017 8:31	65	23/4/2017 17:36	66	24/4/2017 22:41	63	27/3/2017 0:31	53
18/4/2017 22:26	63	21/4/2017 19:31	65	23/4/2017 8:36	64	23/4/2017 17:41	66	24/4/2017 22:46	62	27/3/2017 0:36	60
18/4/2017 22:31	63	21/4/2017 19:36	64	23/4/2017 8:41	64	23/4/2017 17:46	66	24/4/2017 22:51	63	27/3/2017 0:41	61
18/4/2017 22:36	63	21/4/2017 19:41	65	23/4/2017 8:46	63	23/4/2017 17:51	65	24/4/2017 22:56	62	27/3/2017 0:46	60
18/4/2017 22:41	63	21/4/2017 19:46	65	23/4/2017 8:51	63	23/4/2017 17:56	65	25/4/2017 19:01	65	27/3/2017 0:51	60
18/4/2017 22:46	63	21/4/2017 19:51	65	23/4/2017 8:56	65	23/4/2017 18:01	66	25/4/2017 19:06	64	27/3/2017 0:56	60
18/4/2017 22:51	63	21/4/2017 19:56	65	23/4/2017 9:01	64	23/4/2017 18:06	65	25/4/2017 19:11	64	27/3/2017 1:01	61
18/4/2017 22:56	63	21/4/2017 20:01	65	23/4/2017 9:06	64	23/4/2017 18:11	65	25/4/2017 19:16	66	27/3/2017 1:06	60
19/4/2017 19:01	66	21/4/2017 20:06	65	23/4/2017 9:11	64	23/4/2017 18:16	65	25/4/2017 19:21	66	27/3/2017 1:11	60
19/4/2017 19:06	65	21/4/2017 20:11	65	23/4/2017 9:16	65	23/4/2017 18:21	66	25/4/2017 19:26	65	27/3/2017 1:16	60
19/4/2017 19:11	66	21/4/2017 20:16	65	23/4/2017 9:21	64	23/4/2017 18:26	65	25/4/2017 19:31	64	27/3/2017 1:21	60
19/4/2017 19:16	66	21/4/2017 20:21	64	23/4/2017 9:26	64	23/4/2017 18:31	64	25/4/2017 19:36	63	27/3/2017 1:26	59
19/4/2017 19:21	65	21/4/2017 20:26	65	23/4/2017 9:31	63	23/4/2017 18:36	64	25/4/2017 19:41	63	27/3/2017 1:31	58
19/4/2017 19:26	66	21/4/2017 20:31	64	23/4/2017 9:36	64	23/4/2017 18:41	64	25/4/2017 19:46	63	27/3/2017 1:36	58
19/4/2017 19:31	65	21/4/2017 20:36	65	23/4/2017 9:41	64	23/4/2017 18:46	63	25/4/2017 19:51	64	27/3/2017 1:41	59
19/4/2017 19:36	65	21/4/2017 20:41	64	23/4/2017 9:46	64	23/4/2017 18:51	64	25/4/2017 19:56	64	27/3/2017 1:46	57
19/4/2017 19:41	65	21/4/2017 20:46	64	23/4/2017 9:51	63	23/4/2017 18:56	64	25/4/2017 20:01	65	27/3/2017 1:51	58
19/4/2017 19:46	64	21/4/2017 20:51	64	23/4/2017 9:56	64	23/4/2017 19:01	64	25/4/2017 20:06	65	27/3/2017 1:56	59
19/4/2017 19:51	64	21/4/2017 20:56	64	23/4/2017 10:01	64	23/4/2017 19:06	66	25/4/2017 20:11	65	27/3/2017 2:01	58
19/4/2017 19:56	65	21/4/2017 21:01	64	23/4/2017 10:06	64	23/4/2017 19:11	64	25/4/2017 20:16	65	27/3/2017 2:06	59
19/4/2017 20:01	66	21/4/2017 21:06	64	23/4/2017 10:11	64	23/4/2017 19:16	65	25/4/2017 20:21	65	27/3/2017 2:11	59
19/4/2017 20:06	66	21/4/2017 21:11	63	23/4/2017 10:16	64	23/4/2017 19:21	64	25/4/2017 20:26	65	27/3/2017 2:16	58
19/4/2017 20:11	64	21/4/2017 21:16	64	23/4/2017 10:21	65	23/4/2017 19:26	64	25/4/2017 20:31	65	27/3/2017 2:21	58
19/4/2017 20:16	64	21/4/2017 21:21	64	23/4/2017 10:26	64	23/4/2017 19:31	64	25/4/2017 20:36	65	27/3/2017 2:26	58
19/4/2017 20:21	63	21/4/2017 21:26	64	23/4/2017 10:31	64	23/4/2017 19:36	64	25/4/2017 20:41	65	27/3/2017 2:31	58
19/4/2017 20:26	63	21/4/2017 21:31	64	23/4/2017 10:36	63	23/4/2017 19:41	64	25/4/2017 20:46	65	27/3/2017 2:36	57
19/4/2017 20:31	63	21/4/2017 21:36	64	23/4/2017 10:41	64	23/4/2017 19:46	65	25/4/2017 20:51</			

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
27/3/2017 5:41	59	28/3/2017 6:46	61	29/3/2017 23:51	52	31/3/2017 0:56	60	1/4/2017 2:01	43	2/4/2017 3:06	59
27/3/2017 5:46	60	28/3/2017 6:51	60	29/3/2017 23:56	54	31/3/2017 1:01	61	1/4/2017 2:06	53	2/4/2017 3:11	60
27/3/2017 5:51	60	28/3/2017 6:56	58	30/3/2017 0:01	62	31/3/2017 1:06	60	1/4/2017 2:11	62	2/4/2017 3:16	60
27/3/2017 5:56	61	28/3/2017 23:01	58	30/3/2017 0:06	62	31/3/2017 1:11	60	1/4/2017 2:16	61	2/4/2017 3:21	60
27/3/2017 6:01	60	28/3/2017 23:06	53	30/3/2017 0:11	61	31/3/2017 1:16	61	1/4/2017 2:21	49	2/4/2017 3:26	59
27/3/2017 6:06	61	28/3/2017 23:11	58	30/3/2017 0:16	53	31/3/2017 1:21	60	1/4/2017 2:26	62	2/4/2017 3:31	60
27/3/2017 6:11	61	28/3/2017 23:16	55	30/3/2017 0:21	61	31/3/2017 1:26	59	1/4/2017 2:31	62	2/4/2017 3:36	60
27/3/2017 6:16	49	28/3/2017 23:21	52	30/3/2017 0:26	62	31/3/2017 1:31	60	1/4/2017 2:36	46	2/4/2017 3:41	59
27/3/2017 6:21	55	28/3/2017 23:26	48	30/3/2017 0:31	61	31/3/2017 1:36	59	1/4/2017 2:41	61	2/4/2017 3:46	59
27/3/2017 6:26	52	28/3/2017 23:31	52	30/3/2017 0:36	62	31/3/2017 1:41	59	1/4/2017 2:46	62	2/4/2017 3:51	60
27/3/2017 6:31	55	28/3/2017 23:36	62	30/3/2017 0:41	61	31/3/2017 1:46	60	1/4/2017 2:51	62	2/4/2017 3:56	60
27/3/2017 6:36	60	28/3/2017 23:41	62	30/3/2017 0:46	61	31/3/2017 1:51	60	1/4/2017 2:56	62	2/4/2017 4:01	59
27/3/2017 6:41	61	28/3/2017 23:46	53	30/3/2017 0:51	61	31/3/2017 1:56	60	1/4/2017 3:01	61	2/4/2017 4:06	59
27/3/2017 6:46	62	28/3/2017 23:51	62	30/3/2017 0:56	61	31/3/2017 2:01	59	1/4/2017 3:06	61	2/4/2017 4:11	58
27/3/2017 6:51	58	28/3/2017 23:56	62	30/3/2017 1:01	61	31/3/2017 2:06	58	1/4/2017 3:11	60	2/4/2017 4:16	59
27/3/2017 6:56	60	29/3/2017 0:01	61	30/3/2017 1:06	61	31/3/2017 2:11	59	1/4/2017 3:16	61	2/4/2017 4:21	58
27/3/2017 23:01	60	29/3/2017 0:06	62	30/3/2017 1:11	61	31/3/2017 2:16	60	1/4/2017 3:21	59	2/4/2017 4:26	60
27/3/2017 23:06	52	29/3/2017 0:11	61	30/3/2017 1:16	60	31/3/2017 2:21	59	1/4/2017 3:26	60	2/4/2017 4:31	58
27/3/2017 23:11	52	29/3/2017 0:16	62	30/3/2017 1:21	61	31/3/2017 2:26	58	1/4/2017 3:31	62	2/4/2017 4:36	59
27/3/2017 23:16	49	29/3/2017 0:21	62	30/3/2017 1:26	60	31/3/2017 2:31	59	1/4/2017 3:36	60	2/4/2017 4:41	58
27/3/2017 23:21	55	29/3/2017 0:26	61	30/3/2017 1:31	60	31/3/2017 2:36	57	1/4/2017 3:41	60	2/4/2017 4:46	58
27/3/2017 23:26	58	29/3/2017 0:31	61	30/3/2017 1:36	60	31/3/2017 2:41	58	1/4/2017 3:46	60	2/4/2017 4:51	58
27/3/2017 23:31	49	29/3/2017 0:36	60	30/3/2017 1:41	59	31/3/2017 2:46	58	1/4/2017 3:51	61	2/4/2017 4:56	58
27/3/2017 23:36	61	29/3/2017 0:41	60	30/3/2017 1:46	58	31/3/2017 2:51	58	1/4/2017 3:56	59	2/4/2017 5:01	58
27/3/2017 23:41	61	29/3/2017 0:46	60	30/3/2017 1:51	59	31/3/2017 2:56	59	1/4/2017 4:01	60	2/4/2017 5:06	59
27/3/2017 23:46	61	29/3/2017 0:51	59	30/3/2017 1:56	59	31/3/2017 3:01	57	1/4/2017 4:06	60	2/4/2017 5:11	59
27/3/2017 23:51	61	29/3/2017 0:56	60	30/3/2017 2:01	60	31/3/2017 3:06	58	1/4/2017 4:11	59	2/4/2017 5:16	58
27/3/2017 23:56	61	29/3/2017 1:01	60	30/3/2017 2:06	58	31/3/2017 3:11	58	1/4/2017 4:16	60	2/4/2017 5:21	59
28/3/2017 0:01	61	29/3/2017 1:06	60	30/3/2017 2:11	59	31/3/2017 3:16	58	1/4/2017 4:21	60	2/4/2017 5:26	59
28/3/2017 0:06	61	29/3/2017 1:11	59	30/3/2017 2:16	59	31/3/2017 3:21	58	1/4/2017 4:26	60	2/4/2017 5:31	59
28/3/2017 0:11	61	29/3/2017 1:16	60	30/3/2017 2:21	58	31/3/2017 3:26	58	1/4/2017 4:31	61	2/4/2017 5:36	59
28/3/2017 0:16	62	29/3/2017 1:21	59	30/3/2017 2:26	58	31/3/2017 3:31	57	1/4/2017 4:36	58	2/4/2017 5:41	59
28/3/2017 0:21	61	29/3/2017 1:26	60	30/3/2017 2:31	59	31/3/2017 3:36	58	1/4/2017 4:41	60	2/4/2017 5:46	60
28/3/2017 0:26	60	29/3/2017 1:31	59	30/3/2017 2:36	60	31/3/2017 3:41	57	1/4/2017 4:46	60	2/4/2017 5:51	60
28/3/2017 0:31	60	29/3/2017 1:36	58	30/3/2017 2:41	57	31/3/2017 3:46	57	1/4/2017 4:51	59	2/4/2017 5:56	61
28/3/2017 0:36	60	29/3/2017 1:41	59	30/3/2017 2:46	59	31/3/2017 3:51	58	1/4/2017 4:56	59	2/4/2017 6:01	59
28/3/2017 0:41	61	29/3/2017 1:46	59	30/3/2017 2:51	58	31/3/2017 3:56	57	1/4/2017 5:01	60	2/4/2017 6:06	60
28/3/2017 0:46	60	29/3/2017 1:51	58	30/3/2017 2:56	58	31/3/2017 4:01	57	1/4/2017 5:06	60	2/4/2017 6:11	61
28/3/2017 0:51	60	29/3/2017 1:56	58	30/3/2017 3:01	58	31/3/2017 4:06	57	1/4/2017 5:11	60	2/4/2017 6:16	62
28/3/2017 0:56	60	29/3/2017 2:01	58	30/3/2017 3:06	57	31/3/2017 4:11	57	1/4/2017 5:16	59	2/4/2017 6:21	48
28/3/2017 1:01	60	29/3/2017 2:06	59	30/3/2017 3:11	58	31/3/2017 4:16	58	1/4/2017 5:21	60	2/4/2017 6:26	62
28/3/2017 1:06	60	29/3/2017 2:11	58	30/3/2017 3:16	58	31/3/2017 4:21	58	1/4/2017 5:26	61	2/4/2017 6:31	50
28/3/2017 1:11	60	29/3/2017 2:16	58	30/3/2017 3:21	58	31/3/2017 4:26	58	1/4/2017 5:31	62	2/4/2017 6:36	54
28/3/2017 1:16	60	29/3/2017 2:21	60	30/3/2017 3:26	58	31/3/2017 4:31	56	1/4/2017 5:36	60	2/4/2017 6:41	62
28/3/2017 1:21	59	29/3/2017 2:26	57	30/3/2017 3:31	58	31/3/2017 4:36	57	1/4/2017 5:41	61	2/4/2017 6:46	51
28/3/2017 1:26	59	29/3/2017 2:31	58	30/3/2017 3:36	59	31/3/2017 4:41	57	1/4/2017 5:46	61	2/4/2017 6:51	49
28/3/2017 1:31	59	29/3/2017 2:36	58	30/3/2017 3:41	57	31/3/2017 4:46	57	1/4/2017 5:51	61	2/4/2017 6:56	55
28/3/2017 1:36	59	29/3/2017 2:41	58	30/3/2017 3:46	59	31/3/2017 4:51	58	1/4/2017 5:56	61	2/4/2017 23:01	62
28/3/2017 1:41	60	29/3/2017 2:46	57	30/3/2017 3:51	58	31/3/2017 4:56	57	1/4/2017 6:01	61	2/4/2017 23:06	62
28/3/2017 1:46	58	29/3/2017 2:51	58	30/3/2017 3:56	56	31/3/2017 5:01	57	1/4/2017 6:06	61	2/4/2017 23:11	44
28/3/2017 1:51	59	29/3/2017 2:56	58	30/3/2017 4:01	57	31/3/2017 5:06	57	1/4/2017 6:11	62	2/4/2017 23:16	43
28/3/2017 1:56	59	29/3/2017 3:01	56	30/3/2017 4:06	57	31/3/2017 5:11	58	1/4/2017 6:16	46	2/4/2017 23:21	53
28/3/2017 2:01	59	29/3/2017 3:06	57	30/3/2017 4:11	57	31/3/2017 5:16	58	1/4/2017 6:21	57	2/4/2017 23:26	62
28/3/2017 2:06	60	29/3/2017 3:11	56	30/3/2017 4:16	57	31/3/2017 5:21	59	1/4/2017 6:26	57	2/4/2017 23:31	62
28/3/2017 2:11	59	29/3/2017 3:16	56	30/3/2017 4:21	58	31/3/2017 5:26	58	1/4/2017 6:31	56	2/4/2017 23:36	61
28/3/2017 2:16	58	29/3/2017 3:21	56	30/3/2017 4:26	59	31/3/2017 5:31	59	1/4/2017 6:36	60	2/4/2017 23:41	61
28/3/2017 2:21	58	29/3/2017 3:26	57	30/3/2017 4:31	57	31/3/2017 5:36	60	1/4/2017 6:41	59	2/4/2017 23:46	61
28/3/2017 2:26	57	29/3/2017 3:31	58	30/3/2017 4:36	57	31/3/2017 5:41	59	1/4/2017 6:46	58	2/4/2017 23:51	61
28/3/2017 2:31	58	29/3/2017 3:36	58	30/3/2017 4:41	57	31/3/2017 5:46	59	1/4/2017 6:51	60	2/4/2017 23:56	61
28/3/2017 2:36	59	29/3/2017 3:41	58	30/3/2017 4:46	57	31/3/2017 5:51	58	1/4/2017 6:56	58	3/4/2017 0:01	60
28/3/2017 2:41	57	29/3/2017 3:46	57	30/3/2017 4:51	58	31/3/2017 5:56	60	1/4/2017 23:01	54	3/4/2017 0:06	60
28/3/2017 2:46	57	29/3/2017 3:51	58	30/3/2017 4:56	57	31/3/2017 6:01	60	1/4/2017 23:06	54	3/4/2017 0:11	61
28/3/2017 2:51	59	29/3/2017 3:56	57	30/3/2017 5:01	58	31/3/2017 6:06	61	1/4/2017 23:11	52	3/4/2017 0:16	60
28/3/2017 2:56	57	29/3/2017 4:01	58	30/3/2017 5:06	57	31/3/2017 6:11	61	1/4/2017 23:16	55	3/4/2017 0:21	61
28/3/2017 3:01	58	29/3/2017 4:06	58	30/3/2017 5:11	57	31/3/2017 6:16	62	1/4/2017 23:21	47	3/4/2017 0:26	61
28/3/2017 3:06	59	29/3/2017 4:11	58	30/3/2017 5:16	58	31/3/2017 6:21	56	1/4/2017 23:26	56	3/4/2017 0:31	60
28/3/2017 3:11	58	29/3/2017 4:16	57	30/3/2017 5:21	59	31/3/2017 6:26	56	1/4/2017 23:31	55	3/4/2017 0:36	60
28/3/2017 3:16	59	29/3/2017 4:21	57	30/3/2017 5:26	59	31/3/2017 6:31	55	1/4/2017 23:36	55	3/4/2017 0:41	60
28/3/2017 3:21	58	29/3/2017 4:26	58	30/3/2017 5:31	59	31/3/2017 6:36	56	1/4/2017 23:41	54	3/4/2017 0:46	60
28/3/2017 3:26	60	29/3/2017 4:31	57	30/3/2017 5:36	59	31/3/2017 6:41	57	1/4/2017 23:46	53	3/4/2017 0:51	59
28/3/2017 3:31	58	29/3/2017 4:36	57	30/3/2017 5:41	60	31/3/2017 6:46	57	1/4/2017 23:51	51	3/4/2017 0:56	60
28/3/2017 3:36	58	29/3/2017 4:41	57	30/3/2017 5:46	59	31/3/2017 6:51	57	1/4/2017 23:56	53	3/4/2017 1:01	59
28/3/2017 3:41	57	29/3/2017 4:46	57	30/3/2017 5:51	60	31/3/2017 6:56	59	2/4/2017 0:01	60	3/4/2017 1:06	59
28/3/2017 3:46	58	29/3/2017 4:51	58	30/3/2017 5:56	59	31/3/2017 23:01	62	2/4/2017 0:06	49	3/4/2017 1:11	59
28/3/2017 3:51	58	29/3/2017 4:56	58	30/3/2017 6:01	60	31/3/2017 23:06	63	2/4/2017 0:11	52	3/4/2017 1:16	59
28/3/2017 3:56	57	29/3/2017 5:01	57	30/3/2017 6:06	60	31/3/2017 23:11	61	2/4/2017 0:16	62	3/4/2017 1:21	58
28/3/2017 4:01	56	29/3/2017 5:06	58	30/3/2017 6:11	61	31/3/					

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
3/4/2017 4:11	56	4/4/2017 5:16	58	5/4/2017 6:21	62	6/4/2017 23:26	46	8/4/2017 0:31	62	9/4/2017 1:36	60
3/4/2017 4:16	57	4/4/2017 5:21	58	5/4/2017 6:26	53	6/4/2017 23:31	62	8/4/2017 0:36	61	9/4/2017 1:41	60
3/4/2017 4:21	57	4/4/2017 5:26	59	5/4/2017 6:31	59	6/4/2017 23:36	61	8/4/2017 0:41	61	9/4/2017 1:46	60
3/4/2017 4:26	58	4/4/2017 5:31	58	5/4/2017 6:36	57	6/4/2017 23:41	61	8/4/2017 0:46	61	9/4/2017 1:51	59
3/4/2017 4:31	58	4/4/2017 5:36	59	5/4/2017 6:41	60	6/4/2017 23:46	61	8/4/2017 0:51	62	9/4/2017 1:56	59
3/4/2017 4:36	57	4/4/2017 5:41	59	5/4/2017 6:46	59	6/4/2017 23:51	62	8/4/2017 0:56	61	9/4/2017 2:01	59
3/4/2017 4:41	56	4/4/2017 5:46	58	5/4/2017 6:51	55	6/4/2017 23:56	61	8/4/2017 1:01	61	9/4/2017 2:06	59
3/4/2017 4:46	57	4/4/2017 5:51	60	5/4/2017 6:56	56	7/4/2017 0:01	61	8/4/2017 1:06	61	9/4/2017 2:11	60
3/4/2017 4:51	57	4/4/2017 5:56	61	5/4/2017 23:01	52	7/4/2017 0:06	61	8/4/2017 1:11	61	9/4/2017 2:16	60
3/4/2017 4:56	58	4/4/2017 6:01	60	5/4/2017 23:06	46	7/4/2017 0:11	62	8/4/2017 1:16	62	9/4/2017 2:21	60
3/4/2017 5:01	57	4/4/2017 6:06	60	5/4/2017 23:11	43	7/4/2017 0:16	61	8/4/2017 1:21	60	9/4/2017 2:26	60
3/4/2017 5:06	58	4/4/2017 6:11	60	5/4/2017 23:16	43	7/4/2017 0:21	61	8/4/2017 1:26	61	9/4/2017 2:31	59
3/4/2017 5:11	58	4/4/2017 6:16	61	5/4/2017 23:21	48	7/4/2017 0:26	61	8/4/2017 1:31	61	9/4/2017 2:36	59
3/4/2017 5:16	56	4/4/2017 6:21	60	5/4/2017 23:26	62	7/4/2017 0:31	61	8/4/2017 1:36	60	9/4/2017 2:41	58
3/4/2017 5:21	59	4/4/2017 6:26	62	5/4/2017 23:31	54	7/4/2017 0:36	61	8/4/2017 1:41	61	9/4/2017 2:46	59
3/4/2017 5:26	59	4/4/2017 6:31	61	5/4/2017 23:36	52	7/4/2017 0:41	60	8/4/2017 1:46	60	9/4/2017 2:51	58
3/4/2017 5:31	58	4/4/2017 6:36	62	5/4/2017 23:41	62	7/4/2017 0:46	61	8/4/2017 1:51	60	9/4/2017 2:56	58
3/4/2017 5:36	59	4/4/2017 6:41	61	5/4/2017 23:46	62	7/4/2017 0:51	60	8/4/2017 1:56	60	9/4/2017 3:01	59
3/4/2017 5:41	59	4/4/2017 6:46	49	5/4/2017 23:51	53	7/4/2017 0:56	60	8/4/2017 2:01	60	9/4/2017 3:06	58
3/4/2017 5:46	60	4/4/2017 6:51	55	5/4/2017 23:56	61	7/4/2017 1:01	60	8/4/2017 2:06	60	9/4/2017 3:11	59
3/4/2017 5:51	60	4/4/2017 6:56	62	6/4/2017 0:01	61	7/4/2017 1:06	60	8/4/2017 2:11	60	9/4/2017 3:16	60
3/4/2017 5:56	60	4/4/2017 23:01	61	6/4/2017 0:06	62	7/4/2017 1:11	59	8/4/2017 2:16	61	9/4/2017 3:21	58
3/4/2017 6:01	59	4/4/2017 23:06	61	6/4/2017 0:11	61	7/4/2017 1:16	60	8/4/2017 2:21	60	9/4/2017 3:26	59
3/4/2017 6:06	61	4/4/2017 23:11	61	6/4/2017 0:16	61	7/4/2017 1:21	60	8/4/2017 2:26	60	9/4/2017 3:31	60
3/4/2017 6:11	61	4/4/2017 23:16	62	6/4/2017 0:21	55	7/4/2017 1:26	60	8/4/2017 2:31	60	9/4/2017 3:36	60
3/4/2017 6:16	56	4/4/2017 23:21	43	6/4/2017 0:26	62	7/4/2017 1:31	59	8/4/2017 2:36	60	9/4/2017 3:41	62
3/4/2017 6:21	62	4/4/2017 23:26	60	6/4/2017 0:31	62	7/4/2017 1:36	59	8/4/2017 2:41	59	9/4/2017 3:46	59
3/4/2017 6:26	52	4/4/2017 23:31	61	6/4/2017 0:36	61	7/4/2017 1:41	59	8/4/2017 2:46	59	9/4/2017 3:51	58
3/4/2017 6:31	51	4/4/2017 23:36	61	6/4/2017 0:41	61	7/4/2017 1:46	59	8/4/2017 2:51	59	9/4/2017 3:56	57
3/4/2017 6:36	57	4/4/2017 23:41	61	6/4/2017 0:46	60	7/4/2017 1:51	58	8/4/2017 2:56	59	9/4/2017 4:01	58
3/4/2017 6:41	60	4/4/2017 23:46	61	6/4/2017 0:51	60	7/4/2017 1:56	59	8/4/2017 3:01	60	9/4/2017 4:06	58
3/4/2017 6:46	60	4/4/2017 23:51	50	6/4/2017 0:56	60	7/4/2017 2:01	59	8/4/2017 3:06	59	9/4/2017 4:11	59
3/4/2017 6:51	59	4/4/2017 23:56	61	6/4/2017 1:01	59	7/4/2017 2:06	59	8/4/2017 3:11	59	9/4/2017 4:16	58
3/4/2017 6:56	61	5/4/2017 0:01	60	6/4/2017 1:06	60	7/4/2017 2:11	59	8/4/2017 3:16	59	9/4/2017 4:21	59
3/4/2017 23:01	62	5/4/2017 0:06	61	6/4/2017 1:11	60	7/4/2017 2:16	58	8/4/2017 3:21	59	9/4/2017 4:26	59
3/4/2017 23:06	51	5/4/2017 0:11	61	6/4/2017 1:16	60	7/4/2017 2:21	59	8/4/2017 3:26	59	9/4/2017 4:31	58
3/4/2017 23:11	55	5/4/2017 0:16	61	6/4/2017 1:21	60	7/4/2017 2:26	58	8/4/2017 3:31	58	9/4/2017 4:36	58
3/4/2017 23:16	55	5/4/2017 0:21	61	6/4/2017 1:26	59	7/4/2017 2:31	58	8/4/2017 3:36	59	9/4/2017 4:41	58
3/4/2017 23:21	58	5/4/2017 0:26	60	6/4/2017 1:31	59	7/4/2017 2:36	59	8/4/2017 3:41	59	9/4/2017 4:46	58
3/4/2017 23:26	53	5/4/2017 0:31	61	6/4/2017 1:36	59	7/4/2017 2:41	59	8/4/2017 3:46	59	9/4/2017 4:51	57
3/4/2017 23:31	61	5/4/2017 0:36	60	6/4/2017 1:41	58	7/4/2017 2:46	58	8/4/2017 3:51	60	9/4/2017 4:56	58
3/4/2017 23:36	48	5/4/2017 0:41	60	6/4/2017 1:46	66	7/4/2017 2:51	58	8/4/2017 3:56	58	9/4/2017 5:01	58
3/4/2017 23:41	62	5/4/2017 0:46	59	6/4/2017 1:51	58	7/4/2017 2:56	59	8/4/2017 4:01	58	9/4/2017 5:06	58
3/4/2017 23:46	50	5/4/2017 0:51	59	6/4/2017 1:56	58	7/4/2017 3:01	57	8/4/2017 4:06	59	9/4/2017 5:11	57
3/4/2017 23:51	62	5/4/2017 0:56	59	6/4/2017 2:01	58	7/4/2017 3:06	58	8/4/2017 4:11	59	9/4/2017 5:16	58
3/4/2017 23:56	48	5/4/2017 1:01	60	6/4/2017 2:06	59	7/4/2017 3:11	58	8/4/2017 4:16	59	9/4/2017 5:21	59
4/4/2017 0:01	62	5/4/2017 1:06	58	6/4/2017 2:11	58	7/4/2017 3:16	58	8/4/2017 4:21	60	9/4/2017 5:26	59
4/4/2017 0:06	61	5/4/2017 1:11	60	6/4/2017 2:16	58	7/4/2017 3:21	58	8/4/2017 4:26	60	9/4/2017 5:31	59
4/4/2017 0:11	46	5/4/2017 1:16	59	6/4/2017 2:21	58	7/4/2017 3:26	57	8/4/2017 4:31	60	9/4/2017 5:36	59
4/4/2017 0:16	48	5/4/2017 1:21	60	6/4/2017 2:26	58	7/4/2017 3:31	58	8/4/2017 4:36	58	9/4/2017 5:41	59
4/4/2017 0:21	62	5/4/2017 1:26	58	6/4/2017 2:31	58	7/4/2017 3:36	57	8/4/2017 4:41	58	9/4/2017 5:46	59
4/4/2017 0:26	52	5/4/2017 1:31	60	6/4/2017 2:36	58	7/4/2017 3:41	56	8/4/2017 4:46	59	9/4/2017 5:51	60
4/4/2017 0:31	61	5/4/2017 1:36	58	6/4/2017 2:41	57	7/4/2017 3:46	57	8/4/2017 4:51	60	9/4/2017 5:56	60
4/4/2017 0:36	61	5/4/2017 1:41	58	6/4/2017 2:46	57	7/4/2017 3:51	59	8/4/2017 4:56	58	9/4/2017 6:01	61
4/4/2017 0:41	61	5/4/2017 1:46	58	6/4/2017 2:51	59	7/4/2017 3:56	57	8/4/2017 5:01	59	9/4/2017 6:06	60
4/4/2017 0:46	61	5/4/2017 1:51	58	6/4/2017 2:56	58	7/4/2017 4:01	59	8/4/2017 5:06	59	9/4/2017 6:11	61
4/4/2017 0:51	61	5/4/2017 1:56	57	6/4/2017 3:01	58	7/4/2017 4:06	59	8/4/2017 5:11	58	9/4/2017 6:16	61
4/4/2017 0:56	60	5/4/2017 2:01	58	6/4/2017 3:06	57	7/4/2017 4:11	57	8/4/2017 5:16	59	9/4/2017 6:21	62
4/4/2017 1:01	61	5/4/2017 2:06	58	6/4/2017 3:11	58	7/4/2017 4:16	57	8/4/2017 5:21	58	9/4/2017 6:26	55
4/4/2017 1:06	62	5/4/2017 2:11	56	6/4/2017 3:16	57	7/4/2017 4:21	57	8/4/2017 5:26	59	9/4/2017 6:31	62
4/4/2017 1:11	61	5/4/2017 2:16	58	6/4/2017 3:21	56	7/4/2017 4:26	58	8/4/2017 5:31	60	9/4/2017 6:36	61
4/4/2017 1:16	60	5/4/2017 2:21	58	6/4/2017 3:26	58	7/4/2017 4:31	58	8/4/2017 5:36	60	9/4/2017 6:41	61
4/4/2017 1:21	61	5/4/2017 2:26	56	6/4/2017 3:31	56	7/4/2017 4:36	57	8/4/2017 5:41	60	9/4/2017 6:46	61
4/4/2017 1:26	61	5/4/2017 2:31	57	6/4/2017 3:36	58	7/4/2017 4:41	56	8/4/2017 5:46	59	9/4/2017 6:51	61
4/4/2017 1:31	61	5/4/2017 2:36	58	6/4/2017 3:41	57	7/4/2017 4:46	58	8/4/2017 5:51	60	9/4/2017 6:56	44
4/4/2017 1:36	60	5/4/2017 2:41	57	6/4/2017 3:46	56	7/4/2017 4:51	58	8/4/2017 5:56	59	9/4/2017 23:01	61
4/4/2017 1:41	61	5/4/2017 2:46	57	6/4/2017 3:51	57	7/4/2017 4:56	58	8/4/2017 6:01	60	9/4/2017 23:06	61
4/4/2017 1:46	60	5/4/2017 2:51	56	6/4/2017 3:56	56	7/4/2017 5:01	58	8/4/2017 6:06	60	9/4/2017 23:11	62
4/4/2017 1:51	60	5/4/2017 2:56	58	6/4/2017 4:01	56	7/4/2017 5:06	58	8/4/2017 6:11	62	9/4/2017 23:16	61
4/4/2017 1:56	60	5/4/2017 3:01	55	6/4/2017 4:06	57	7/4/2017 5:11	58	8/4/2017 6:16	61	9/4/2017 23:21	61
4/4/2017 2:01	60	5/4/2017 3:06	57	6/4/2017 4:11	56	7/4/2017 5:16	58	8/4/2017 6:21	43	9/4/2017 23:26	62
4/4/2017 2:06	60	5/4/2017 3:11	58	6/4/2017 4:16	57	7/4/2017 5:21	58	8/4/2017 6:26	53	9/4/2017 23:31	61
4/4/2017 2:11	60	5/4/2017 3:16	56	6/4/2017 4:21	56	7/4/2017 5:26	59	8/4/2017 6:31	57	9/4/2017 23:36	61
4/4/2017 2:16	59	5/4/2017 3:21	57	6/4/2017 4:26	57	7/4/2017 5:31	59	8/4/2017 6:36	59	9/4/2017 23:41	61
4/4/2017 2:21	59	5/4/2017 3:26	58	6/4/2017 4:31	57	7/4/2017 5:36	59	8/4/2017 6:41	61	9/4/2017 23:46	61
4/4/2017 2:26	59	5/4/2017 3:31	56	6/4/2017 4:36	58	7/4/2017 5:41	60	8/4/2017 6:46	57	9/4/2017 23:51	61
4/4/2017 2:31	61	5/4/2017 3:36	57	6/4/2017 4:41	58	7/4/2017 5:46	60	8/4/2017 6:51	55	9/4/2017 23:56	60
4/4/2017 2:36	59	5/4/2017 3:41	56	6/4/2017 4:46	57	7/4/2017 5:51	61	8/4/2017 6:56	56	10/4/2017 0:01	61
4/4/2017 2:41	60	5/4/2017 3:46	57	6/4/2017 4:51	57						

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
10/4/2017 2:41	58	11/4/2017 3:46	58	12/4/2017 4:51	58	13/4/2017 5:56	61	14/4/2017 23:01	56	16/4/2017 0:06	61
10/4/2017 2:46	57	11/4/2017 3:51	59	12/4/2017 4:56	59	13/4/2017 6:01	61	14/4/2017 23:06	62	16/4/2017 0:11	61
10/4/2017 2:51	57	11/4/2017 3:56	57	12/4/2017 5:01	58	13/4/2017 6:06	61	14/4/2017 23:11	62	16/4/2017 0:16	61
10/4/2017 2:56	57	11/4/2017 4:01	58	12/4/2017 5:06	58	13/4/2017 6:11	62	14/4/2017 23:16	55	16/4/2017 0:21	60
10/4/2017 3:01	57	11/4/2017 4:06	57	12/4/2017 5:11	59	13/4/2017 6:16	43	14/4/2017 23:21	52	16/4/2017 0:26	60
10/4/2017 3:06	57	11/4/2017 4:11	57	12/4/2017 5:16	59	13/4/2017 6:21	48	14/4/2017 23:26	62	16/4/2017 0:31	60
10/4/2017 3:11	56	11/4/2017 4:16	58	12/4/2017 5:21	60	13/4/2017 6:26	54	14/4/2017 23:31	56	16/4/2017 0:36	60
10/4/2017 3:16	56	11/4/2017 4:21	59	12/4/2017 5:26	60	13/4/2017 6:31	56	14/4/2017 23:36	62	16/4/2017 0:41	60
10/4/2017 3:21	56	11/4/2017 4:26	58	12/4/2017 5:31	60	13/4/2017 6:36	60	14/4/2017 23:41	43	16/4/2017 0:46	60
10/4/2017 3:26	58	11/4/2017 4:31	58	12/4/2017 5:36	60	13/4/2017 6:41	61	14/4/2017 23:46	62	16/4/2017 0:51	60
10/4/2017 3:31	58	11/4/2017 4:36	57	12/4/2017 5:41	60	13/4/2017 6:46	60	14/4/2017 23:51	61	16/4/2017 0:56	59
10/4/2017 3:36	58	11/4/2017 4:41	57	12/4/2017 5:46	60	13/4/2017 6:51	61	14/4/2017 23:56	61	16/4/2017 1:01	60
10/4/2017 3:41	57	11/4/2017 4:46	58	12/4/2017 5:51	60	13/4/2017 6:56	60	15/4/2017 0:01	62	16/4/2017 1:06	60
10/4/2017 3:46	57	11/4/2017 4:51	59	12/4/2017 5:56	60	13/4/2017 23:01	59	15/4/2017 0:06	62	16/4/2017 1:11	52
10/4/2017 3:51	58	11/4/2017 4:56	58	12/4/2017 6:01	60	13/4/2017 23:06	58	15/4/2017 0:11	61	16/4/2017 1:16	59
10/4/2017 3:56	56	11/4/2017 5:01	59	12/4/2017 6:06	62	13/4/2017 23:11	55	15/4/2017 0:16	60	16/4/2017 1:21	60
10/4/2017 4:01	57	11/4/2017 5:06	59	12/4/2017 6:11	47	13/4/2017 23:16	55	15/4/2017 0:21	60	16/4/2017 1:26	60
10/4/2017 4:06	57	11/4/2017 5:11	58	12/4/2017 6:16	46	13/4/2017 23:21	56	15/4/2017 0:26	60	16/4/2017 1:31	60
10/4/2017 4:11	57	11/4/2017 5:16	59	12/4/2017 6:21	49	13/4/2017 23:26	55	15/4/2017 0:31	60	16/4/2017 1:36	60
10/4/2017 4:16	57	11/4/2017 5:21	60	12/4/2017 6:26	56	13/4/2017 23:31	56	15/4/2017 0:36	60	16/4/2017 1:41	60
10/4/2017 4:21	58	11/4/2017 5:26	60	12/4/2017 6:31	53	13/4/2017 23:36	55	15/4/2017 0:41	61	16/4/2017 1:46	59
10/4/2017 4:26	56	11/4/2017 5:31	60	12/4/2017 6:36	58	13/4/2017 23:41	62	15/4/2017 0:46	60	16/4/2017 1:51	59
10/4/2017 4:31	57	11/4/2017 5:36	60	12/4/2017 6:41	60	13/4/2017 23:46	54	15/4/2017 0:51	59	16/4/2017 1:56	59
10/4/2017 4:36	58	11/4/2017 5:41	60	12/4/2017 6:46	61	13/4/2017 23:51	55	15/4/2017 0:56	60	16/4/2017 2:01	58
10/4/2017 4:41	57	11/4/2017 5:46	60	12/4/2017 6:51	62	13/4/2017 23:56	56	15/4/2017 1:01	59	16/4/2017 2:06	60
10/4/2017 4:46	57	11/4/2017 5:51	60	12/4/2017 6:56	63	14/4/2017 0:01	62	15/4/2017 1:06	60	16/4/2017 2:11	59
10/4/2017 4:51	58	11/4/2017 5:56	61	12/4/2017 23:01	57	14/4/2017 0:06	61	15/4/2017 1:11	63	16/4/2017 2:16	60
10/4/2017 4:56	57	11/4/2017 6:01	61	12/4/2017 23:06	60	14/4/2017 0:11	62	15/4/2017 1:16	60	16/4/2017 2:21	60
10/4/2017 5:01	59	11/4/2017 6:06	61	12/4/2017 23:11	56	14/4/2017 0:16	61	15/4/2017 1:21	60	16/4/2017 2:26	60
10/4/2017 5:06	58	11/4/2017 6:11	54	12/4/2017 23:16	56	14/4/2017 0:21	62	15/4/2017 1:26	60	16/4/2017 2:31	59
10/4/2017 5:11	58	11/4/2017 6:16	55	12/4/2017 23:21	56	14/4/2017 0:26	61	15/4/2017 1:31	59	16/4/2017 2:36	60
10/4/2017 5:16	58	11/4/2017 6:21	57	12/4/2017 23:26	58	14/4/2017 0:31	61	15/4/2017 1:36	59	16/4/2017 2:41	59
10/4/2017 5:21	59	11/4/2017 6:26	54	12/4/2017 23:31	56	14/4/2017 0:36	61	15/4/2017 1:41	59	16/4/2017 2:46	59
10/4/2017 5:26	59	11/4/2017 6:31	60	12/4/2017 23:36	53	14/4/2017 0:41	61	15/4/2017 1:46	59	16/4/2017 2:51	59
10/4/2017 5:31	58	11/4/2017 6:36	59	12/4/2017 23:41	58	14/4/2017 0:46	61	15/4/2017 1:51	60	16/4/2017 2:56	59
10/4/2017 5:36	59	11/4/2017 6:41	60	12/4/2017 23:46	54	14/4/2017 0:51	61	15/4/2017 1:56	54	16/4/2017 3:01	59
10/4/2017 5:41	59	11/4/2017 6:46	60	12/4/2017 23:51	54	14/4/2017 0:56	61	15/4/2017 2:01	60	16/4/2017 3:06	58
10/4/2017 5:46	60	11/4/2017 6:51	60	12/4/2017 23:56	53	14/4/2017 1:01	61	15/4/2017 2:06	59	16/4/2017 3:11	58
10/4/2017 5:51	59	11/4/2017 6:56	61	13/4/2017 0:01	62	14/4/2017 1:06	61	15/4/2017 2:11	58	16/4/2017 3:16	60
10/4/2017 5:56	59	11/4/2017 23:01	58	13/4/2017 0:06	55	14/4/2017 1:11	61	15/4/2017 2:16	59	16/4/2017 3:21	59
10/4/2017 6:01	60	11/4/2017 23:06	60	13/4/2017 0:11	48	14/4/2017 1:16	61	15/4/2017 2:21	59	16/4/2017 3:26	58
10/4/2017 6:06	61	11/4/2017 23:11	59	13/4/2017 0:16	54	14/4/2017 1:21	61	15/4/2017 2:26	58	16/4/2017 3:31	60
10/4/2017 6:11	61	11/4/2017 23:16	58	13/4/2017 0:21	62	14/4/2017 1:26	61	15/4/2017 2:31	59	16/4/2017 3:36	60
10/4/2017 6:16	61	11/4/2017 23:21	58	13/4/2017 0:26	62	14/4/2017 1:31	61	15/4/2017 2:36	59	16/4/2017 3:41	58
10/4/2017 6:21	62	11/4/2017 23:26	57	13/4/2017 0:31	61	14/4/2017 1:36	60	15/4/2017 2:41	58	16/4/2017 3:46	58
10/4/2017 6:26	49	11/4/2017 23:31	57	13/4/2017 0:36	61	14/4/2017 1:41	61	15/4/2017 2:46	58	16/4/2017 3:51	59
10/4/2017 6:31	56	11/4/2017 23:36	56	13/4/2017 0:41	60	14/4/2017 1:46	60	15/4/2017 2:51	58	16/4/2017 3:56	58
10/4/2017 6:36	57	11/4/2017 23:41	57	13/4/2017 0:46	61	14/4/2017 1:51	60	15/4/2017 2:56	58	16/4/2017 4:01	59
10/4/2017 6:41	57	11/4/2017 23:46	55	13/4/2017 0:51	61	14/4/2017 1:56	60	15/4/2017 3:01	59	16/4/2017 4:06	58
10/4/2017 6:46	59	11/4/2017 23:51	47	13/4/2017 0:56	61	14/4/2017 2:01	60	15/4/2017 3:06	58	16/4/2017 4:11	59
10/4/2017 6:51	58	11/4/2017 23:56	50	13/4/2017 1:01	61	14/4/2017 2:06	61	15/4/2017 3:11	58	16/4/2017 4:16	57
10/4/2017 6:56	59	12/4/2017 0:01	62	13/4/2017 1:06	62	14/4/2017 2:11	60	15/4/2017 3:16	58	16/4/2017 4:21	59
10/4/2017 23:01	52	12/4/2017 0:06	62	13/4/2017 1:11	61	14/4/2017 2:16	60	15/4/2017 3:21	59	16/4/2017 4:26	59
10/4/2017 23:06	54	12/4/2017 0:11	62	13/4/2017 1:16	60	14/4/2017 2:21	60	15/4/2017 3:26	58	16/4/2017 4:31	57
10/4/2017 23:11	50	12/4/2017 0:16	61	13/4/2017 1:21	61	14/4/2017 2:26	60	15/4/2017 3:31	58	16/4/2017 4:36	57
10/4/2017 23:16	48	12/4/2017 0:21	62	13/4/2017 1:26	60	14/4/2017 2:31	59	15/4/2017 3:36	59	16/4/2017 4:41	57
10/4/2017 23:21	61	12/4/2017 0:26	62	13/4/2017 1:31	61	14/4/2017 2:36	59	15/4/2017 3:41	60	16/4/2017 4:46	58
10/4/2017 23:26	62	12/4/2017 0:31	61	13/4/2017 1:36	61	14/4/2017 2:41	61	15/4/2017 3:46	58	16/4/2017 4:51	59
10/4/2017 23:31	54	12/4/2017 0:36	61	13/4/2017 1:41	60	14/4/2017 2:46	60	15/4/2017 3:51	59	16/4/2017 4:56	58
10/4/2017 23:36	61	12/4/2017 0:41	61	13/4/2017 1:46	60	14/4/2017 2:51	60	15/4/2017 3:56	58	16/4/2017 5:01	59
10/4/2017 23:41	62	12/4/2017 0:46	60	13/4/2017 1:51	60	14/4/2017 2:56	60	15/4/2017 4:01	58	16/4/2017 5:06	58
10/4/2017 23:46	61	12/4/2017 0:51	61	13/4/2017 1:56	60	14/4/2017 3:01	59	15/4/2017 4:06	58	16/4/2017 5:11	58
10/4/2017 23:51	61	12/4/2017 0:56	61	13/4/2017 2:01	60	14/4/2017 3:06	60	15/4/2017 4:11	58	16/4/2017 5:16	58
10/4/2017 23:56	61	12/4/2017 1:01	61	13/4/2017 2:06	59	14/4/2017 3:11	59	15/4/2017 4:16	58	16/4/2017 5:21	59
11/4/2017 0:01	61	12/4/2017 1:06	60	13/4/2017 2:11	61	14/4/2017 3:16	59	15/4/2017 4:21	59	16/4/2017 5:26	59
11/4/2017 0:06	61	12/4/2017 1:11	60	13/4/2017 2:16	59	14/4/2017 3:21	60	15/4/2017 4:26	61	16/4/2017 5:31	58
11/4/2017 0:11	61	12/4/2017 1:16	60	13/4/2017 2:21	60	14/4/2017 3:26	59	15/4/2017 4:31	59	16/4/2017 5:36	58
11/4/2017 0:16	60	12/4/2017 1:21	61	13/4/2017 2:26	59	14/4/2017 3:31	60	15/4/2017 4:36	58	16/4/2017 5:41	58
11/4/2017 0:21	60	12/4/2017 1:26	60	13/4/2017 2:31	59	14/4/2017 3:36	59	15/4/2017 4:41	58	16/4/2017 5:46	59
11/4/2017 0:26	60	12/4/2017 1:31	61	13/4/2017 2:36	60	14/4/2017 3:41	59	15/4/2017 4:46	58	16/4/2017 5:51	59
11/4/2017 0:31	61	12/4/2017 1:36	60	13/4/2017 2:41	58	14/4/2017 3:46	59	15/4/2017 4:51	60	16/4/2017 5:56	60
11/4/2017 0:36	60	12/4/2017 1:41	59	13/4/2017 2:46	59	14/4/2017 3:51	58	15/4/2017 4:56	58	16/4/2017 6:01	60
11/4/2017 0:41	60	12/4/2017 1:46	59	13/4/2017 2:51	58	14/4/2017 3:56	59	15/4/2017 5:01	59	16/4/2017 6:06	60
11/4/2017 0:46	60	12/4/2017 1:51	58	13/4/2017 2:56	60	14/4/2017 4:01	60	15/4/2017 5:06	60	16/4/2017 6:11	61
11/4/2017 0:51	60	12/4/2017 1:56	60	13/4/2017 3:01	58	14/4/2017 4:06	59	15/4/2017 5:11	58	16/4/2017 6:16	60
11/4/2017 0:56	60	12/4/2017 2:01	60	13/4/2017 3:06	59	14/4/20					

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
17/4/2017 1:11	60	18/4/2017 2:16	57	19/4/2017 3:21	56	20/4/2017 4:26	57	21/4/2017 5:31	58	22/4/2017 6:36	44
17/4/2017 1:16	60	18/4/2017 2:21	58	19/4/2017 3:26	57	20/4/2017 4:31	58	21/4/2017 5:36	59	22/4/2017 6:41	56
17/4/2017 1:21	60	18/4/2017 2:26	59	19/4/2017 3:31	58	20/4/2017 4:36	57	21/4/2017 5:41	59	22/4/2017 6:46	54
17/4/2017 1:26	59	18/4/2017 2:31	57	19/4/2017 3:36	58	20/4/2017 4:41	58	21/4/2017 5:46	60	22/4/2017 6:51	58
17/4/2017 1:31	60	18/4/2017 2:36	59	19/4/2017 3:41	57	20/4/2017 4:46	57	21/4/2017 5:51	59	22/4/2017 6:56	55
17/4/2017 1:36	59	18/4/2017 2:41	57	19/4/2017 3:46	58	20/4/2017 4:51	58	21/4/2017 5:56	59	22/4/2017 23:01	57
17/4/2017 1:41	60	18/4/2017 2:46	57	19/4/2017 3:51	57	20/4/2017 4:56	58	21/4/2017 6:01	60	22/4/2017 23:06	57
17/4/2017 1:46	59	18/4/2017 2:51	58	19/4/2017 3:56	57	20/4/2017 5:01	57	21/4/2017 6:06	60	22/4/2017 23:11	55
17/4/2017 1:51	58	18/4/2017 2:56	57	19/4/2017 4:01	57	20/4/2017 5:06	58	21/4/2017 6:11	61	22/4/2017 23:16	56
17/4/2017 1:56	59	18/4/2017 3:01	57	19/4/2017 4:06	57	20/4/2017 5:11	58	21/4/2017 6:16	62	22/4/2017 23:21	55
17/4/2017 2:01	59	18/4/2017 3:06	57	19/4/2017 4:11	58	20/4/2017 5:16	59	21/4/2017 6:21	61	22/4/2017 23:26	54
17/4/2017 2:06	58	18/4/2017 3:11	56	19/4/2017 4:16	57	20/4/2017 5:21	58	21/4/2017 6:26	50	22/4/2017 23:31	57
17/4/2017 2:11	59	18/4/2017 3:16	56	19/4/2017 4:21	57	20/4/2017 5:26	59	21/4/2017 6:31	54	22/4/2017 23:36	54
17/4/2017 2:16	59	18/4/2017 3:21	57	19/4/2017 4:26	57	20/4/2017 5:31	59	21/4/2017 6:36	53	22/4/2017 23:41	56
17/4/2017 2:21	59	18/4/2017 3:26	56	19/4/2017 4:31	58	20/4/2017 5:36	59	21/4/2017 6:41	54	22/4/2017 23:46	62
17/4/2017 2:26	62	18/4/2017 3:31	57	19/4/2017 4:36	57	20/4/2017 5:41	59	21/4/2017 6:46	58	22/4/2017 23:51	52
17/4/2017 2:31	59	18/4/2017 3:36	57	19/4/2017 4:41	56	20/4/2017 5:46	59	21/4/2017 6:51	59	22/4/2017 23:56	50
17/4/2017 2:36	60	18/4/2017 3:41	57	19/4/2017 4:46	57	20/4/2017 5:51	59	21/4/2017 6:56	58	23/4/2017 0:01	55
17/4/2017 2:41	59	18/4/2017 3:46	57	19/4/2017 4:51	57	20/4/2017 5:56	59	21/4/2017 23:01	58	23/4/2017 0:06	57
17/4/2017 2:46	58	18/4/2017 3:51	57	19/4/2017 4:56	57	20/4/2017 6:01	60	21/4/2017 23:06	58	23/4/2017 0:11	48
17/4/2017 2:51	58	18/4/2017 3:56	56	19/4/2017 5:01	57	20/4/2017 6:06	61	21/4/2017 23:11	56	23/4/2017 0:16	42
17/4/2017 2:56	58	18/4/2017 4:01	55	19/4/2017 5:06	59	20/4/2017 6:11	61	21/4/2017 23:16	58	23/4/2017 0:21	58
17/4/2017 3:01	58	18/4/2017 4:06	57	19/4/2017 5:11	58	20/4/2017 6:16	61	21/4/2017 23:21	58	23/4/2017 0:26	61
17/4/2017 3:06	58	18/4/2017 4:11	58	19/4/2017 5:16	57	20/4/2017 6:21	61	21/4/2017 23:26	55	23/4/2017 0:31	62
17/4/2017 3:11	57	18/4/2017 4:16	57	19/4/2017 5:21	59	20/4/2017 6:26	49	21/4/2017 23:31	57	23/4/2017 0:36	56
17/4/2017 3:16	58	18/4/2017 4:21	57	19/4/2017 5:26	58	20/4/2017 6:31	51	21/4/2017 23:36	58	23/4/2017 0:41	45
17/4/2017 3:21	58	18/4/2017 4:26	58	19/4/2017 5:31	60	20/4/2017 6:36	56	21/4/2017 23:41	59	23/4/2017 0:46	61
17/4/2017 3:26	58	18/4/2017 4:31	59	19/4/2017 5:36	59	20/4/2017 6:41	55	21/4/2017 23:46	58	23/4/2017 0:51	61
17/4/2017 3:31	57	18/4/2017 4:36	57	19/4/2017 5:41	60	20/4/2017 6:46	58	21/4/2017 23:51	56	23/4/2017 0:56	61
17/4/2017 3:36	57	18/4/2017 4:41	57	19/4/2017 5:46	59	20/4/2017 6:51	59	21/4/2017 23:56	56	23/4/2017 1:01	61
17/4/2017 3:41	57	18/4/2017 4:46	58	19/4/2017 5:51	60	20/4/2017 6:56	57	22/4/2017 0:01	52	23/4/2017 1:06	61
17/4/2017 3:46	57	18/4/2017 4:51	58	19/4/2017 5:56	60	20/4/2017 23:01	56	22/4/2017 0:06	53	23/4/2017 1:11	61
17/4/2017 3:51	58	18/4/2017 4:56	58	19/4/2017 6:01	61	20/4/2017 23:06	57	22/4/2017 0:11	51	23/4/2017 1:16	61
17/4/2017 3:56	57	18/4/2017 5:01	56	19/4/2017 6:06	61	20/4/2017 23:11	51	22/4/2017 0:16	54	23/4/2017 1:21	61
17/4/2017 4:01	56	18/4/2017 5:06	58	19/4/2017 6:11	61	20/4/2017 23:16	56	22/4/2017 0:21	52	23/4/2017 1:26	60
17/4/2017 4:06	58	18/4/2017 5:11	57	19/4/2017 6:16	61	20/4/2017 23:21	54	22/4/2017 0:26	51	23/4/2017 1:31	61
17/4/2017 4:11	57	18/4/2017 5:16	58	19/4/2017 6:21	59	20/4/2017 23:26	51	22/4/2017 0:31	53	23/4/2017 1:36	60
17/4/2017 4:16	58	18/4/2017 5:21	58	19/4/2017 6:26	52	20/4/2017 23:31	49	22/4/2017 0:36	51	23/4/2017 1:41	61
17/4/2017 4:21	57	18/4/2017 5:26	57	19/4/2017 6:31	55	20/4/2017 23:36	62	22/4/2017 0:41	61	23/4/2017 1:46	60
17/4/2017 4:26	59	18/4/2017 5:31	59	19/4/2017 6:36	53	20/4/2017 23:41	62	22/4/2017 0:46	49	23/4/2017 1:51	60
17/4/2017 4:31	57	18/4/2017 5:36	59	19/4/2017 6:41	59	20/4/2017 23:46	52	22/4/2017 0:51	48	23/4/2017 1:56	60
17/4/2017 4:36	58	18/4/2017 5:41	59	19/4/2017 6:46	57	20/4/2017 23:51	47	22/4/2017 0:56	44	23/4/2017 2:01	60
17/4/2017 4:41	57	18/4/2017 5:46	60	19/4/2017 6:51	59	20/4/2017 23:56	45	22/4/2017 1:01	62	23/4/2017 2:06	61
17/4/2017 4:46	57	18/4/2017 5:51	60	19/4/2017 6:56	60	21/4/2017 0:01	62	22/4/2017 1:06	62	23/4/2017 2:11	60
17/4/2017 4:51	58	18/4/2017 5:56	60	19/4/2017 23:01	45	21/4/2017 0:06	62	22/4/2017 1:11	61	23/4/2017 2:16	60
17/4/2017 4:56	58	18/4/2017 6:01	60	19/4/2017 23:06	62	21/4/2017 0:11	61	22/4/2017 1:16	62	23/4/2017 2:21	60
17/4/2017 5:01	57	18/4/2017 6:06	61	19/4/2017 23:11	52	21/4/2017 0:16	61	22/4/2017 1:21	61	23/4/2017 2:26	59
17/4/2017 5:06	59	18/4/2017 6:11	62	19/4/2017 23:16	50	21/4/2017 0:21	61	22/4/2017 1:26	62	23/4/2017 2:31	60
17/4/2017 5:11	58	18/4/2017 6:16	62	19/4/2017 23:21	56	21/4/2017 0:26	61	22/4/2017 1:31	61	23/4/2017 2:36	60
17/4/2017 5:16	58	18/4/2017 6:21	62	19/4/2017 23:26	61	21/4/2017 0:31	61	22/4/2017 1:36	61	23/4/2017 2:41	60
17/4/2017 5:21	59	18/4/2017 6:26	50	19/4/2017 23:31	62	21/4/2017 0:36	61	22/4/2017 1:41	61	23/4/2017 2:46	61
17/4/2017 5:26	58	18/4/2017 6:31	58	19/4/2017 23:36	62	21/4/2017 0:41	60	22/4/2017 1:46	61	23/4/2017 2:51	60
17/4/2017 5:31	58	18/4/2017 6:36	57	19/4/2017 23:41	61	21/4/2017 0:46	60	22/4/2017 1:51	60	23/4/2017 2:56	60
17/4/2017 5:36	59	18/4/2017 6:41	59	19/4/2017 23:46	62	21/4/2017 0:51	60	22/4/2017 1:56	61	23/4/2017 3:01	59
17/4/2017 5:41	58	18/4/2017 6:46	60	19/4/2017 23:51	61	21/4/2017 0:56	60	22/4/2017 2:01	61	23/4/2017 3:06	59
17/4/2017 5:46	59	18/4/2017 6:51	59	19/4/2017 23:56	61	21/4/2017 1:01	59	22/4/2017 2:06	61	23/4/2017 3:11	59
17/4/2017 5:51	60	18/4/2017 6:56	60	20/4/2017 0:01	62	21/4/2017 1:06	60	22/4/2017 2:11	60	23/4/2017 3:16	59
17/4/2017 5:56	58	18/4/2017 23:01	56	20/4/2017 0:06	61	21/4/2017 1:11	60	22/4/2017 2:16	61	23/4/2017 3:21	60
17/4/2017 6:01	59	18/4/2017 23:06	62	20/4/2017 0:11	61	21/4/2017 1:16	60	22/4/2017 2:21	60	23/4/2017 3:26	60
17/4/2017 6:06	61	18/4/2017 23:11	62	20/4/2017 0:16	60	21/4/2017 1:21	60	22/4/2017 2:26	61	23/4/2017 3:31	59
17/4/2017 6:11	60	18/4/2017 23:16	51	20/4/2017 0:21	54	21/4/2017 1:26	60	22/4/2017 2:31	61	23/4/2017 3:36	60
17/4/2017 6:16	60	18/4/2017 23:21	62	20/4/2017 0:26	61	21/4/2017 1:31	59	22/4/2017 2:36	60	23/4/2017 3:41	58
17/4/2017 6:21	60	18/4/2017 23:26	61	20/4/2017 0:31	61	21/4/2017 1:36	59	22/4/2017 2:41	61	23/4/2017 3:46	60
17/4/2017 6:26	47	18/4/2017 23:31	62	20/4/2017 0:36	62	21/4/2017 1:41	59	22/4/2017 2:46	61	23/4/2017 3:51	59
17/4/2017 6:31	62	18/4/2017 23:36	62	20/4/2017 0:41	60	21/4/2017 1:46	59	22/4/2017 2:51	60	23/4/2017 3:56	67
17/4/2017 6:36	56	18/4/2017 23:41	62	20/4/2017 0:46	60	21/4/2017 1:51	59	22/4/2017 2:56	60	23/4/2017 4:01	59
17/4/2017 6:41	57	18/4/2017 23:46	61	20/4/2017 0:51	60	21/4/2017 1:56	58	22/4/2017 3:01	59	23/4/2017 4:06	59
17/4/2017 6:46	61	18/4/2017 23:51	62	20/4/2017 0:56	60	21/4/2017 2:01	59	22/4/2017 3:06	60	23/4/2017 4:11	59
17/4/2017 6:51	61	18/4/2017 23:56	61	20/4/2017 1:01	59	21/4/2017 2:06	59	22/4/2017 3:11	60	23/4/2017 4:16	59
17/4/2017 6:56	61	19/4/2017 0:01	61	20/4/2017 1:06	60	21/4/2017 2:11	59	22/4/2017 3:16	59	23/4/2017 4:21	59
17/4/2017 23:01	61	19/4/2017 0:06	61	20/4/2017 1:11	60	21/4/2017 2:16	59	22/4/2017 3:21	60	23/4/2017 4:26	59
17/4/2017 23:06	61	19/4/2017 0:11	61	20/4/2017 1:16	59	21/4/2017 2:21	58	22/4/2017 3:26	60	23/4/2017 4:31	60
17/4/2017 23:11	62	19/4/2017 0:16	60	20/4/2017 1:21	59	21/4/2017 2:26	58	22/4/2017 3:31	59	23/4/2017 4:36	60
17/4/2017 23:16	62	19/4/2017 0:21	60	20/4/2017 1:26	59	21/4/2017 2:31	58	22/4/2017 3:36	59	23/4/2017 4:41	59
17/4/2017 23:21	62	19/4/2017 0:26	60	20/4/2017 1:31	60	21/4/2017 2:36	58	22/4/2017 3:41	59	23/4/2017 4:46	58
17/4/2017 23:26	61	19/4/2017 0:31	61	20/4/2017 1:36	59	2					

Real-time Noise Data	RTN1 (Food and Environmental Hygiene Department Depot)	
23/4/2017 23:41 62	25/4/2017 0:46 60	26/4/2017 1:51 60
23/4/2017 23:46 61	25/4/2017 0:51 61	26/4/2017 1:56 60
23/4/2017 23:51 61	25/4/2017 0:56 60	26/4/2017 2:01 59
23/4/2017 23:56 61	25/4/2017 1:01 60	26/4/2017 2:06 59
24/4/2017 0:01 60	25/4/2017 1:06 60	26/4/2017 2:11 59
24/4/2017 0:06 61	25/4/2017 1:11 59	26/4/2017 2:16 59
24/4/2017 0:11 61	25/4/2017 1:16 60	26/4/2017 2:21 58
24/4/2017 0:16 61	25/4/2017 1:21 61	26/4/2017 2:26 59
24/4/2017 0:21 61	25/4/2017 1:26 60	26/4/2017 2:31 59
24/4/2017 0:26 62	25/4/2017 1:31 59	26/4/2017 2:36 58
24/4/2017 0:31 61	25/4/2017 1:36 59	26/4/2017 2:41 59
24/4/2017 0:36 60	25/4/2017 1:41 60	26/4/2017 2:46 58
24/4/2017 0:41 59	25/4/2017 1:46 58	26/4/2017 2:51 59
24/4/2017 0:46 61	25/4/2017 1:51 58	26/4/2017 2:56 59
24/4/2017 0:51 60	25/4/2017 1:56 58	26/4/2017 3:01 58
24/4/2017 0:56 59	25/4/2017 2:01 58	26/4/2017 3:06 59
24/4/2017 1:01 60	25/4/2017 2:06 58	26/4/2017 3:11 59
24/4/2017 1:06 60	25/4/2017 2:11 58	26/4/2017 3:16 59
24/4/2017 1:11 61	25/4/2017 2:16 58	26/4/2017 3:21 58
24/4/2017 1:16 60	25/4/2017 2:21 58	26/4/2017 3:26 57
24/4/2017 1:21 60	25/4/2017 2:26 58	26/4/2017 3:31 59
24/4/2017 1:26 59	25/4/2017 2:31 58	26/4/2017 3:36 59
24/4/2017 1:31 59	25/4/2017 2:36 58	26/4/2017 3:41 57
24/4/2017 1:36 59	25/4/2017 2:41 58	26/4/2017 3:46 57
24/4/2017 1:41 58	25/4/2017 2:46 57	26/4/2017 3:51 58
24/4/2017 1:46 58	25/4/2017 2:51 57	26/4/2017 3:56 58
24/4/2017 1:51 59	25/4/2017 2:56 57	26/4/2017 4:01 58
24/4/2017 1:56 58	25/4/2017 3:01 58	26/4/2017 4:06 58
24/4/2017 2:01 59	25/4/2017 3:06 56	26/4/2017 4:11 58
24/4/2017 2:06 58	25/4/2017 3:11 58	26/4/2017 4:16 58
24/4/2017 2:11 57	25/4/2017 3:16 57	26/4/2017 4:21 58
24/4/2017 2:16 58	25/4/2017 3:21 57	26/4/2017 4:26 59
24/4/2017 2:21 58	25/4/2017 3:26 57	26/4/2017 4:31 59
24/4/2017 2:26 58	25/4/2017 3:31 57	26/4/2017 4:36 58
24/4/2017 2:31 58	25/4/2017 3:36 58	26/4/2017 4:41 57
24/4/2017 2:36 59	25/4/2017 3:41 57	26/4/2017 4:46 58
24/4/2017 2:41 58	25/4/2017 3:46 57	26/4/2017 4:51 59
24/4/2017 2:46 56	25/4/2017 3:51 57	26/4/2017 4:56 59
24/4/2017 2:51 59	25/4/2017 3:56 57	26/4/2017 5:01 59
24/4/2017 2:56 58	25/4/2017 4:01 56	26/4/2017 5:06 59
24/4/2017 3:01 58	25/4/2017 4:06 58	26/4/2017 5:11 59
24/4/2017 3:06 57	25/4/2017 4:11 56	26/4/2017 5:16 60
24/4/2017 3:11 57	25/4/2017 4:16 56	26/4/2017 5:21 59
24/4/2017 3:16 57	25/4/2017 4:21 57	26/4/2017 5:26 59
24/4/2017 3:21 57	25/4/2017 4:26 57	26/4/2017 5:31 60
24/4/2017 3:26 58	25/4/2017 4:31 57	26/4/2017 5:36 61
24/4/2017 3:31 57	25/4/2017 4:36 57	26/4/2017 5:41 60
24/4/2017 3:36 58	25/4/2017 4:41 57	26/4/2017 5:46 61
24/4/2017 3:41 56	25/4/2017 4:46 57	26/4/2017 5:51 49
24/4/2017 3:46 57	25/4/2017 4:51 57	26/4/2017 5:56 61
24/4/2017 3:51 57	25/4/2017 4:56 58	26/4/2017 6:01 61
24/4/2017 3:56 57	25/4/2017 5:01 57	26/4/2017 6:06 61
24/4/2017 4:01 56	25/4/2017 5:06 57	26/4/2017 6:11 54
24/4/2017 4:06 57	25/4/2017 5:11 59	26/4/2017 6:16 55
24/4/2017 4:11 57	25/4/2017 5:16 58	26/4/2017 6:21 54
24/4/2017 4:16 58	25/4/2017 5:21 57	26/4/2017 6:26 56
24/4/2017 4:21 58	25/4/2017 5:26 59	26/4/2017 6:31 58
24/4/2017 4:26 58	25/4/2017 5:31 59	26/4/2017 6:36 59
24/4/2017 4:31 57	25/4/2017 5:36 59	26/4/2017 6:41 61
24/4/2017 4:36 57	25/4/2017 5:41 59	26/4/2017 6:46 61
24/4/2017 4:41 57	25/4/2017 5:46 60	26/4/2017 6:51 61
24/4/2017 4:46 57	25/4/2017 5:51 55	26/4/2017 6:56 60
24/4/2017 4:51 60	25/4/2017 5:56 60	26/4/2017 23:01 58
24/4/2017 4:56 58	25/4/2017 6:01 60	26/4/2017 23:06 61
24/4/2017 5:01 58	25/4/2017 6:06 61	26/4/2017 23:11 60
24/4/2017 5:06 59	25/4/2017 6:11 61	26/4/2017 23:16 57
24/4/2017 5:11 58	25/4/2017 6:16 47	26/4/2017 23:21 59
24/4/2017 5:16 58	25/4/2017 6:21 42	26/4/2017 23:26 59
24/4/2017 5:21 59	25/4/2017 6:26 56	26/4/2017 23:31 54
24/4/2017 5:26 59	25/4/2017 6:31 50	26/4/2017 23:36 58
24/4/2017 5:31 59	25/4/2017 6:36 58	26/4/2017 23:41 50
24/4/2017 5:36 60	25/4/2017 6:41 60	26/4/2017 23:46 52
24/4/2017 5:41 60	25/4/2017 6:46 60	26/4/2017 23:51 52
24/4/2017 5:46 60	25/4/2017 6:51 60	26/4/2017 23:56 51
24/4/2017 5:51 61	25/4/2017 6:56 59	
24/4/2017 5:56 61	25/4/2017 23:01 59	
24/4/2017 6:01 61	25/4/2017 23:06 58	
24/4/2017 6:06 62	25/4/2017 23:11 58	
24/4/2017 6:11 62	25/4/2017 23:16 56	
24/4/2017 6:16 49	25/4/2017 23:21 57	
24/4/2017 6:21 54	25/4/2017 23:26 57	
24/4/2017 6:26 57	25/4/2017 23:31 55	
24/4/2017 6:31 59	25/4/2017 23:36 53	
24/4/2017 6:36 60	25/4/2017 23:41 56	
24/4/2017 6:41 59	25/4/2017 23:46 55	
24/4/2017 6:46 61	25/4/2017 23:51 47	
24/4/2017 6:51 60	25/4/2017 23:56 53	
24/4/2017 6:56 58	26/4/2017 0:01 39	
24/4/2017 23:01 56	26/4/2017 0:06 62	
24/4/2017 23:06 52	26/4/2017 0:11 46	
24/4/2017 23:11 48	26/4/2017 0:16 54	
24/4/2017 23:16 49	26/4/2017 0:21 62	
24/4/2017 23:21 52	26/4/2017 0:26 62	
24/4/2017 23:26 62	26/4/2017 0:31 61	
24/4/2017 23:31 62	26/4/2017 0:36 61	
24/4/2017 23:36 52	26/4/2017 0:41 62	
24/4/2017 23:41 49	26/4/2017 0:46 61	
24/4/2017 23:46 62	26/4/2017 0:51 60	
24/4/2017 23:51 54	26/4/2017 0:56 61	
24/4/2017 23:56 62	26/4/2017 1:01 61	
25/4/2017 0:01 61	26/4/2017 1:06 61	
25/4/2017 0:06 61	26/4/2017 1:11 61	
25/4/2017 0:11 61	26/4/2017 1:16 61	
25/4/2017 0:16 61	26/4/2017 1:21 60	
25/4/2017 0:21 61	26/4/2017 1:26 60	
25/4/2017 0:26 61	26/4/2017 1:31 61	
25/4/2017 0:31 61	26/4/2017 1:36 59	
25/4/2017 0:36 60	26/4/2017 1:41 61	
25/4/2017 0:41 60	26/4/2017 1:46 60	

[illegible]

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
28/3/2017 22:56	56	31/3/2017 20:01	57	2/4/2017 9:06	57	2/4/2017 18:11	60	4/4/2017 7:16	55	4/4/2017 16:21	58
29/3/2017 19:01	57	31/3/2017 20:06	58	2/4/2017 9:11	56	2/4/2017 18:16	58	4/4/2017 7:21	56	4/4/2017 16:26	59
29/3/2017 19:06	57	31/3/2017 20:11	58	2/4/2017 9:16	57	2/4/2017 18:21	57	4/4/2017 7:26	54	4/4/2017 16:31	56
29/3/2017 19:11	45	31/3/2017 20:16	61	2/4/2017 9:21	56	2/4/2017 18:26	57	4/4/2017 7:31	55	4/4/2017 16:36	58
29/3/2017 19:16	57	31/3/2017 20:21	62	2/4/2017 9:26	56	2/4/2017 18:31	58	4/4/2017 7:36	55	4/4/2017 16:41	58
29/3/2017 19:21	57	31/3/2017 20:26	56	2/4/2017 9:31	57	2/4/2017 18:36	58	4/4/2017 7:41	55	4/4/2017 16:46	59
29/3/2017 19:26	58	31/3/2017 20:31	57	2/4/2017 9:36	58	2/4/2017 18:41	60	4/4/2017 7:46	56	4/4/2017 16:51	59
29/3/2017 19:31	58	31/3/2017 20:36	58	2/4/2017 9:41	58	2/4/2017 18:46	58	4/4/2017 7:51	46	4/4/2017 16:56	60
29/3/2017 19:36	59	31/3/2017 20:41	58	2/4/2017 9:46	57	2/4/2017 18:51	61	4/4/2017 7:56	56	4/4/2017 17:01	60
29/3/2017 19:41	61	31/3/2017 20:46	61	2/4/2017 9:51	58	2/4/2017 18:56	57	4/4/2017 8:01	59	4/4/2017 17:06	58
29/3/2017 19:46	61	31/3/2017 20:51	59	2/4/2017 9:56	57	2/4/2017 19:01	57	4/4/2017 8:06	57	4/4/2017 17:11	57
29/3/2017 19:51	60	31/3/2017 20:56	58	2/4/2017 10:01	58	2/4/2017 19:06	58	4/4/2017 8:11	58	4/4/2017 17:16	58
29/3/2017 19:56	58	31/3/2017 21:01	60	2/4/2017 10:06	56	2/4/2017 19:11	57	4/4/2017 8:16	57	4/4/2017 17:21	59
29/3/2017 20:01	59	31/3/2017 21:06	58	2/4/2017 10:11	58	2/4/2017 19:16	56	4/4/2017 8:21	57	4/4/2017 17:26	58
29/3/2017 20:06	56	31/3/2017 21:11	57	2/4/2017 10:16	58	2/4/2017 19:21	56	4/4/2017 8:26	56	4/4/2017 17:31	57
29/3/2017 20:11	56	31/3/2017 21:16	58	2/4/2017 10:21	59	2/4/2017 19:26	0	4/4/2017 8:31	57	4/4/2017 17:36	58
29/3/2017 20:16	62	31/3/2017 21:21	59	2/4/2017 10:26	57	2/4/2017 19:31	0	4/4/2017 8:36	58	4/4/2017 17:41	58
29/3/2017 20:21	57	31/3/2017 21:26	58	2/4/2017 10:31	57	2/4/2017 19:36	0	4/4/2017 8:41	56	4/4/2017 17:46	58
29/3/2017 20:26	58	31/3/2017 21:31	57	2/4/2017 10:36	57	2/4/2017 19:41	0	4/4/2017 8:46	56	4/4/2017 17:51	57
29/3/2017 20:31	57	31/3/2017 21:36	57	2/4/2017 10:41	59	2/4/2017 19:46	0	4/4/2017 8:51	57	4/4/2017 17:56	58
29/3/2017 20:36	57	31/3/2017 21:41	57	2/4/2017 10:46	57	2/4/2017 19:51	55	4/4/2017 8:56	56	4/4/2017 18:01	59
29/3/2017 20:41	56	31/3/2017 21:46	60	2/4/2017 10:51	57	2/4/2017 19:56	56	4/4/2017 9:01	56	4/4/2017 18:06	58
29/3/2017 20:46	58	31/3/2017 21:51	57	2/4/2017 10:56	57	2/4/2017 20:01	55	4/4/2017 9:06	58	4/4/2017 18:11	56
29/3/2017 20:51	56	31/3/2017 21:56	59	2/4/2017 11:01	62	2/4/2017 20:06	55	4/4/2017 9:11	58	4/4/2017 18:16	58
29/3/2017 20:56	58	31/3/2017 22:01	57	2/4/2017 11:06	57	2/4/2017 20:11	56	4/4/2017 9:16	57	4/4/2017 18:21	57
29/3/2017 21:01	55	31/3/2017 22:06	59	2/4/2017 11:11	58	2/4/2017 20:16	57	4/4/2017 9:21	57	4/4/2017 18:26	60
29/3/2017 21:06	57	31/3/2017 22:11	59	2/4/2017 11:16	57	2/4/2017 20:21	61	4/4/2017 9:26	56	4/4/2017 18:31	57
29/3/2017 21:11	57	31/3/2017 22:16	58	2/4/2017 11:21	56	2/4/2017 20:26	59	4/4/2017 9:31	57	4/4/2017 18:36	58
29/3/2017 21:16	55	31/3/2017 22:21	59	2/4/2017 11:26	56	2/4/2017 20:31	61	4/4/2017 9:36	58	4/4/2017 18:41	58
29/3/2017 21:21	56	31/3/2017 22:26	56	2/4/2017 11:31	57	2/4/2017 20:36	59	4/4/2017 9:41	57	4/4/2017 18:46	60
29/3/2017 21:26	56	31/3/2017 22:31	60	2/4/2017 11:36	57	2/4/2017 20:41	56	4/4/2017 9:46	57	4/4/2017 18:51	59
29/3/2017 21:31	56	31/3/2017 22:36	58	2/4/2017 11:41	57	2/4/2017 20:46	55	4/4/2017 9:51	57	4/4/2017 18:56	59
29/3/2017 21:36	58	31/3/2017 22:41	56	2/4/2017 11:46	57	2/4/2017 20:51	57	4/4/2017 9:56	57	4/4/2017 19:01	57
29/3/2017 21:41	58	31/3/2017 22:46	57	2/4/2017 11:51	58	2/4/2017 20:56	56	4/4/2017 10:01	57	4/4/2017 19:06	57
29/3/2017 21:46	58	31/3/2017 22:51	60	2/4/2017 11:56	57	2/4/2017 21:01	56	4/4/2017 10:06	58	4/4/2017 19:11	60
29/3/2017 21:51	56	31/3/2017 22:56	55	2/4/2017 12:01	57	2/4/2017 21:06	57	4/4/2017 10:11	57	4/4/2017 19:16	57
29/3/2017 21:56	57	1/4/2017 19:01	57	2/4/2017 12:06	58	2/4/2017 21:11	55	4/4/2017 10:16	57	4/4/2017 19:21	57
29/3/2017 22:01	56	1/4/2017 19:06	58	2/4/2017 12:11	55	2/4/2017 21:16	55	4/4/2017 10:21	58	4/4/2017 19:26	58
29/3/2017 22:06	56	1/4/2017 19:11	57	2/4/2017 12:16	58	2/4/2017 21:21	57	4/4/2017 10:26	58	4/4/2017 19:31	61
29/3/2017 22:11	56	1/4/2017 19:16	57	2/4/2017 12:21	59	2/4/2017 21:26	56	4/4/2017 10:31	60	4/4/2017 19:36	59
29/3/2017 22:16	56	1/4/2017 19:21	58	2/4/2017 12:26	57	2/4/2017 21:31	56	4/4/2017 10:36	58	4/4/2017 19:41	60
29/3/2017 22:21	57	1/4/2017 19:26	57	2/4/2017 12:31	57	2/4/2017 21:36	56	4/4/2017 10:41	60	4/4/2017 19:46	61
29/3/2017 22:26	57	1/4/2017 19:31	57	2/4/2017 12:36	56	2/4/2017 21:41	56	4/4/2017 10:46	58	4/4/2017 19:51	57
29/3/2017 22:31	56	1/4/2017 19:36	61	2/4/2017 12:41	58	2/4/2017 21:46	56	4/4/2017 10:51	59	4/4/2017 19:56	58
29/3/2017 22:36	55	1/4/2017 19:41	59	2/4/2017 12:46	57	2/4/2017 21:51	55	4/4/2017 10:56	57	4/4/2017 20:01	59
29/3/2017 22:41	56	1/4/2017 19:46	60	2/4/2017 12:51	60	2/4/2017 21:56	56	4/4/2017 11:01	59	4/4/2017 20:06	58
29/3/2017 22:46	58	1/4/2017 19:51	62	2/4/2017 12:56	57	2/4/2017 22:01	58	4/4/2017 11:06	57	4/4/2017 20:11	57
29/3/2017 22:51	57	1/4/2017 19:56	56	2/4/2017 13:01	60	2/4/2017 22:06	58	4/4/2017 11:11	58	4/4/2017 20:16	59
29/3/2017 22:56	55	1/4/2017 20:01	56	2/4/2017 13:06	57	2/4/2017 22:11	55	4/4/2017 11:16	58	4/4/2017 20:21	56
30/3/2017 19:01	58	1/4/2017 20:06	58	2/4/2017 13:11	56	2/4/2017 22:16	59	4/4/2017 11:21	57	4/4/2017 20:26	59
30/3/2017 19:06	59	1/4/2017 20:11	57	2/4/2017 13:16	58	2/4/2017 22:21	55	4/4/2017 11:26	58	4/4/2017 20:31	57
30/3/2017 19:11	58	1/4/2017 20:16	60	2/4/2017 13:21	59	2/4/2017 22:26	57	4/4/2017 11:31	56	4/4/2017 20:36	58
30/3/2017 19:16	60	1/4/2017 20:21	57	2/4/2017 13:26	58	2/4/2017 22:31	56	4/4/2017 11:36	56	4/4/2017 20:41	58
30/3/2017 19:21	58	1/4/2017 20:26	58	2/4/2017 13:31	58	2/4/2017 22:36	55	4/4/2017 11:41	58	4/4/2017 20:46	57
30/3/2017 19:26	58	1/4/2017 20:31	59	2/4/2017 13:36	56	2/4/2017 22:41	55	4/4/2017 11:46	57	4/4/2017 20:51	59
30/3/2017 19:31	57	1/4/2017 20:36	58	2/4/2017 13:41	57	2/4/2017 22:46	55	4/4/2017 11:51	58	4/4/2017 20:56	58
30/3/2017 19:36	58	1/4/2017 20:41	59	2/4/2017 13:46	58	2/4/2017 22:51	56	4/4/2017 11:56	58	4/4/2017 21:01	60
30/3/2017 19:41	57	1/4/2017 20:46	57	2/4/2017 13:51	57	2/4/2017 22:56	56	4/4/2017 12:01	57	4/4/2017 21:06	58
30/3/2017 19:46	57	1/4/2017 20:51	57	2/4/2017 13:56	57	3/4/2017 19:01	58	4/4/2017 12:06	56	4/4/2017 21:11	58
30/3/2017 19:51	57	1/4/2017 20:56	60	2/4/2017 14:01	55	3/4/2017 19:06	57	4/4/2017 12:11	59	4/4/2017 21:16	56
30/3/2017 19:56	58	1/4/2017 21:01	59	2/4/2017 14:06	56	3/4/2017 19:11	56	4/4/2017 12:16	62	4/4/2017 21:21	60
30/3/2017 20:01	60	1/4/2017 21:06	57	2/4/2017 14:11	56	3/4/2017 19:16	60	4/4/2017 12:21	58	4/4/2017 21:26	56
30/3/2017 20:06	57	1/4/2017 21:11	56	2/4/2017 14:16	57	3/4/2017 19:21	58	4/4/2017 12:26	56	4/4/2017 21:31	56
30/3/2017 20:11	57	1/4/2017 21:16	57	2/4/2017 14:21	0	3/4/2017 19:26	60	4/4/2017 12:31	56	4/4/2017 21:36	56
30/3/2017 20:16	58	1/4/2017 21:21	62	2/4/2017 14:26	0	3/4/2017 19:31	59	4/4/2017 12:36	57	4/4/2017 21:41	59
30/3/2017 20:21	58	1/4/2017 21:26	57	2/4/2017 14:31	0	3/4/2017 19:36	60	4/4/2017 12:41	58	4/4/2017 21:46	55
30/3/2017 20:26	57	1/4/2017 21:31	56	2/4/2017 14:36	0	3/4/2017 19:41	58	4/4/2017 12:46	58	4/4/2017 21:51	57
30/3/2017 20:31	58	1/4/2017 21:36	56	2/4/2017 14:41	0	3/4/2017 19:46	58	4/4/2017 12:51	52	4/4/2017 21:56	55
30/3/2017 20:36	58	1/4/2017 21:41	57	2/4/2017 14:46	0	3/4/2017 19:51	57	4/4/2017 12:56	61	4/4/2017 22:01	56
30/3/2017 20:41	58	1/4/2017 21:46	57	2/4/2017 14:51	0	3/4/2017 19:56	59	4/4/2017 13:01	57	4/4/2017 22:06	56
30/3/2017 20:46	60	1/4/2017 21:51	56	2/4/2017 14:56	0	3/4/2017 20:01	58	4/4/2017 13:06	57	4/4/2017 22:11	56
30/3/2017 20:51	56	1/4/2017 21:56	57	2/4/2017 15:01	0	3/4/2017 20:06	56	4/4/2017 13:11	59	4/4/2017 22:16	57
30/3/2017 20:56	56	1/4/2017 22:01	57	2/4/2017 15:06	0	3/4/2017 20:11	62	4/4/2017 13:16	59	4/4/2017 22:21	57
30/3/2017 21:01	57	1/4/2017 22:06	59	2/4/2017 15:11	0	3/4/2017 20:16	59	4/4/2017 13:21	59	4/4/2017 22:26	55
30/3/2017 21:06	56	1/4/2017 22:11	57	2/4/2017 15:16	0	3/4/2017 20:21	58	4/4/2017 13:26	58	4/4/2017 22:31	56
30/3/2017 21:11	57	1/4/2017 22:16	58	2/4/2017 15:21	0</						

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
5/4/2017 21:26	57	7/4/2017 22:31	59	9/4/2017 11:36	58	9/4/2017 20:41	58	11/4/2017 21:46	58	13/4/2017 22:51	58
5/4/2017 21:31	56	7/4/2017 22:36	61	9/4/2017 11:41	58	9/4/2017 20:46	59	11/4/2017 21:51	58	13/4/2017 22:56	58
5/4/2017 21:36	60	7/4/2017 22:41	57	9/4/2017 11:46	57	9/4/2017 20:51	58	11/4/2017 21:56	58	14/4/2017 7:01	59
5/4/2017 21:41	58	7/4/2017 22:46	58	9/4/2017 11:51	57	9/4/2017 20:56	57	11/4/2017 22:01	58	14/4/2017 7:06	60
5/4/2017 21:46	62	7/4/2017 22:51	58	9/4/2017 11:56	58	9/4/2017 21:01	57	11/4/2017 22:06	58	14/4/2017 7:11	59
5/4/2017 21:51	56	7/4/2017 22:56	59	9/4/2017 12:01	58	9/4/2017 21:06	57	11/4/2017 22:11	58	14/4/2017 7:16	60
5/4/2017 21:56	56	8/4/2017 19:01	58	9/4/2017 12:06	56	9/4/2017 21:11	57	11/4/2017 22:16	57	14/4/2017 7:21	58
5/4/2017 22:01	58	8/4/2017 19:06	57	9/4/2017 12:11	57	9/4/2017 21:16	58	11/4/2017 22:21	58	14/4/2017 7:26	58
5/4/2017 22:06	59	8/4/2017 19:11	58	9/4/2017 12:16	57	9/4/2017 21:21	57	11/4/2017 22:26	58	14/4/2017 7:31	57
5/4/2017 22:11	57	8/4/2017 19:16	58	9/4/2017 12:21	58	9/4/2017 21:26	57	11/4/2017 22:31	57	14/4/2017 7:36	58
5/4/2017 22:16	56	8/4/2017 19:21	60	9/4/2017 12:26	58	9/4/2017 21:31	58	11/4/2017 22:36	58	14/4/2017 7:41	60
5/4/2017 22:21	56	8/4/2017 19:26	60	9/4/2017 12:31	57	9/4/2017 21:36	58	11/4/2017 22:41	58	14/4/2017 7:46	60
5/4/2017 22:26	56	8/4/2017 19:31	59	9/4/2017 12:36	57	9/4/2017 21:41	58	11/4/2017 22:46	60	14/4/2017 7:51	59
5/4/2017 22:31	58	8/4/2017 19:36	59	9/4/2017 12:41	59	9/4/2017 21:46	58	11/4/2017 22:51	58	14/4/2017 7:56	57
5/4/2017 22:36	55	8/4/2017 19:41	58	9/4/2017 12:46	58	9/4/2017 21:51	58	11/4/2017 22:56	59	14/4/2017 8:01	58
5/4/2017 22:41	55	8/4/2017 19:46	58	9/4/2017 12:51	58	9/4/2017 21:56	57	12/4/2017 19:01	60	14/4/2017 8:06	58
5/4/2017 22:46	56	8/4/2017 19:51	58	9/4/2017 12:56	58	9/4/2017 22:01	57	12/4/2017 19:06	62	14/4/2017 8:11	59
5/4/2017 22:51	56	8/4/2017 19:56	58	9/4/2017 13:01	59	9/4/2017 22:06	57	12/4/2017 19:11	59	14/4/2017 8:16	58
5/4/2017 22:56	54	8/4/2017 20:01	58	9/4/2017 13:06	58	9/4/2017 22:11	57	12/4/2017 19:16	59	14/4/2017 8:21	59
6/4/2017 19:01	59	8/4/2017 20:06	58	9/4/2017 13:11	57	9/4/2017 22:16	57	12/4/2017 19:21	59	14/4/2017 8:26	59
6/4/2017 19:06	56	8/4/2017 20:11	57	9/4/2017 13:16	58	9/4/2017 22:21	57	12/4/2017 19:26	58	14/4/2017 8:31	59
6/4/2017 19:11	59	8/4/2017 20:16	59	9/4/2017 13:21	58	9/4/2017 22:26	57	12/4/2017 19:31	60	14/4/2017 8:36	59
6/4/2017 19:16	58	8/4/2017 20:21	58	9/4/2017 13:26	58	9/4/2017 22:31	58	12/4/2017 19:36	59	14/4/2017 8:41	60
6/4/2017 19:21	60	8/4/2017 20:26	58	9/4/2017 13:31	57	9/4/2017 22:36	58	12/4/2017 19:41	60	14/4/2017 8:46	61
6/4/2017 19:26	58	8/4/2017 20:31	59	9/4/2017 13:36	58	9/4/2017 22:41	57	12/4/2017 19:46	60	14/4/2017 8:51	60
6/4/2017 19:31	60	8/4/2017 20:36	58	9/4/2017 13:41	58	9/4/2017 22:46	57	12/4/2017 19:51	60	14/4/2017 8:56	60
6/4/2017 19:36	60	8/4/2017 20:41	57	9/4/2017 13:46	59	9/4/2017 22:51	57	12/4/2017 19:56	59	14/4/2017 9:01	61
6/4/2017 19:41	58	8/4/2017 20:46	58	9/4/2017 13:51	58	9/4/2017 22:56	57	12/4/2017 20:01	59	14/4/2017 9:06	60
6/4/2017 19:46	57	8/4/2017 20:51	59	9/4/2017 13:56	57	10/4/2017 19:01	59	12/4/2017 20:06	59	14/4/2017 9:11	61
6/4/2017 19:51	57	8/4/2017 20:56	59	9/4/2017 14:01	57	10/4/2017 19:06	59	12/4/2017 20:11	60	14/4/2017 9:16	60
6/4/2017 19:56	60	8/4/2017 21:01	61	9/4/2017 14:06	58	10/4/2017 19:11	60	12/4/2017 20:16	54	14/4/2017 9:21	61
6/4/2017 20:01	57	8/4/2017 21:06	59	9/4/2017 14:11	58	10/4/2017 19:16	60	12/4/2017 20:21	59	14/4/2017 9:26	60
6/4/2017 20:06	56	8/4/2017 21:11	57	9/4/2017 14:16	58	10/4/2017 19:21	59	12/4/2017 20:26	58	14/4/2017 9:31	60
6/4/2017 20:11	58	8/4/2017 21:16	58	9/4/2017 14:21	58	10/4/2017 19:26	59	12/4/2017 20:31	60	14/4/2017 9:36	60
6/4/2017 20:16	57	8/4/2017 21:21	57	9/4/2017 14:26	57	10/4/2017 19:31	59	12/4/2017 20:36	62	14/4/2017 9:41	60
6/4/2017 20:21	58	8/4/2017 21:26	59	9/4/2017 14:31	58	10/4/2017 19:36	60	12/4/2017 20:41	60	14/4/2017 9:46	60
6/4/2017 20:26	57	8/4/2017 21:31	59	9/4/2017 14:36	58	10/4/2017 19:41	59	12/4/2017 20:46	54	14/4/2017 9:51	60
6/4/2017 20:31	58	8/4/2017 21:36	58	9/4/2017 14:41	58	10/4/2017 19:46	59	12/4/2017 20:51	62	14/4/2017 9:56	61
6/4/2017 20:36	58	8/4/2017 21:41	58	9/4/2017 14:46	58	10/4/2017 19:51	59	12/4/2017 20:56	61	14/4/2017 10:01	59
6/4/2017 20:41	57	8/4/2017 21:46	60	9/4/2017 14:51	57	10/4/2017 19:56	60	12/4/2017 21:01	60	14/4/2017 10:06	59
6/4/2017 20:46	56	8/4/2017 21:51	57	9/4/2017 14:56	59	10/4/2017 20:01	60	12/4/2017 21:06	59	14/4/2017 10:11	59
6/4/2017 20:51	57	8/4/2017 21:56	58	9/4/2017 15:01	58	10/4/2017 20:06	59	12/4/2017 21:11	60	14/4/2017 10:16	59
6/4/2017 20:56	59	8/4/2017 22:01	58	9/4/2017 15:06	58	10/4/2017 20:11	59	12/4/2017 21:16	57	14/4/2017 10:21	60
6/4/2017 21:01	59	8/4/2017 22:06	58	9/4/2017 15:11	59	10/4/2017 20:16	59	12/4/2017 21:21	60	14/4/2017 10:26	60
6/4/2017 21:06	57	8/4/2017 22:11	57	9/4/2017 15:16	59	10/4/2017 20:21	59	12/4/2017 21:26	57	14/4/2017 10:31	60
6/4/2017 21:11	57	8/4/2017 22:16	58	9/4/2017 15:21	60	10/4/2017 20:26	59	12/4/2017 21:31	58	14/4/2017 10:36	60
6/4/2017 21:16	58	8/4/2017 22:21	60	9/4/2017 15:26	58	10/4/2017 20:31	60	12/4/2017 21:36	59	14/4/2017 10:41	59
6/4/2017 21:21	55	8/4/2017 22:26	57	9/4/2017 15:31	59	10/4/2017 20:36	59	12/4/2017 21:41	58	14/4/2017 10:46	58
6/4/2017 21:26	56	8/4/2017 22:31	58	9/4/2017 15:36	58	10/4/2017 20:41	59	12/4/2017 21:46	58	14/4/2017 10:51	61
6/4/2017 21:31	61	8/4/2017 22:36	62	9/4/2017 15:41	58	10/4/2017 20:46	59	12/4/2017 21:51	59	14/4/2017 10:56	60
6/4/2017 21:36	57	8/4/2017 22:41	58	9/4/2017 15:46	57	10/4/2017 20:51	59	12/4/2017 21:56	59	14/4/2017 11:01	60
6/4/2017 21:41	60	8/4/2017 22:46	57	9/4/2017 15:51	57	10/4/2017 20:56	59	12/4/2017 22:01	59	14/4/2017 11:06	60
6/4/2017 21:46	57	8/4/2017 22:51	58	9/4/2017 15:56	58	10/4/2017 21:01	60	12/4/2017 22:06	61	14/4/2017 11:11	61
6/4/2017 21:51	56	8/4/2017 22:56	56	9/4/2017 16:01	58	10/4/2017 21:06	59	12/4/2017 22:11	59	14/4/2017 11:16	60
6/4/2017 21:56	56	9/4/2017 7:01	57	9/4/2017 16:06	58	10/4/2017 21:11	60	12/4/2017 22:16	58	14/4/2017 11:21	58
6/4/2017 22:01	58	9/4/2017 7:06	57	9/4/2017 16:11	59	10/4/2017 21:16	59	12/4/2017 22:21	58	14/4/2017 11:26	58
6/4/2017 22:06	56	9/4/2017 7:11	56	9/4/2017 16:16	58	10/4/2017 21:21	59	12/4/2017 22:26	58	14/4/2017 11:31	59
6/4/2017 22:11	58	9/4/2017 7:16	56	9/4/2017 16:21	58	10/4/2017 21:26	58	12/4/2017 22:31	58	14/4/2017 11:36	58
6/4/2017 22:16	57	9/4/2017 7:21	56	9/4/2017 16:26	59	10/4/2017 21:31	58	12/4/2017 22:36	58	14/4/2017 11:41	58
6/4/2017 22:21	57	9/4/2017 7:26	57	9/4/2017 16:31	61	10/4/2017 21:36	58	12/4/2017 22:41	59	14/4/2017 11:46	59
6/4/2017 22:26	56	9/4/2017 7:31	58	9/4/2017 16:36	60	10/4/2017 21:41	59	12/4/2017 22:46	58	14/4/2017 11:51	58
6/4/2017 22:31	56	9/4/2017 7:36	56	9/4/2017 16:41	59	10/4/2017 21:46	59	12/4/2017 22:51	58	14/4/2017 11:56	58
6/4/2017 22:36	55	9/4/2017 7:41	56	9/4/2017 16:46	58	10/4/2017 21:51	59	12/4/2017 22:56	58	14/4/2017 12:01	58
6/4/2017 22:41	55	9/4/2017 7:46	59	9/4/2017 16:51	59	10/4/2017 21:56	59	13/4/2017 19:01	58	14/4/2017 12:06	59
6/4/2017 22:46	57	9/4/2017 7:51	58	9/4/2017 16:56	58	10/4/2017 22:01	59	13/4/2017 19:06	58	14/4/2017 12:11	59
6/4/2017 22:51	58	9/4/2017 7:56	59	9/4/2017 17:01	58	10/4/2017 22:06	59	13/4/2017 19:11	59	14/4/2017 12:16	59
6/4/2017 22:56	57	9/4/2017 8:01	58	9/4/2017 17:06	58	10/4/2017 22:11	59	13/4/2017 19:16	59	14/4/2017 12:21	59
7/4/2017 19:01	59	9/4/2017 8:06	57	9/4/2017 17:11	58	10/4/2017 22:16	60	13/4/2017 19:21	59	14/4/2017 12:26	59
7/4/2017 19:06	60	9/4/2017 8:11	57	9/4/2017 17:16	58	10/4/2017 22:21	59	13/4/2017 19:26	58	14/4/2017 12:31	58
7/4/2017 19:11	53	9/4/2017 8:16	58	9/4/2017 17:21	59	10/4/2017 22:26	59	13/4/2017 19:31	59	14/4/2017 12:36	58
7/4/2017 19:16	60	9/4/2017 8:21	59	9/4/2017 17:26	58	10/4/2017 22:31	59	13/4/2017 19:36	47	14/4/2017 12:41	58
7/4/2017 19:21	58	9/4/2017 8:26	58	9/4/2017 17:31	58	10/4/2017 22:36	59	13/4/2017 19:41	60	14/4/2017 12:46	58
7/4/2017 19:26	60	9/4/2017 8:31	57	9/4/2017 17:36	58	10/4/2017 22:41	59	13/4/2017 19:46	60	14/4/2017 12:51	58
7/4/2017 19:31	58	9/4/2017 8:36	58	9/4/2017 17:41	57	10/4/2017 22:46	59	13/4/2017 19:51	60	14/4/2017 12:56	59
7/4/2017 19:36	61	9/4/2017 8:41	57	9/4/2017 17:46	57	10/4/2017 22:51	58	13/4/2017 19:56	59	14/4/2017 13:01</	

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)					
14/4/2017 15:56	60	15/4/2017 9:01	59	15/4/2017 18:06	59	16/4/2017 11:11	57
14/4/2017 16:01	60	15/4/2017 9:06	59	15/4/2017 18:11	58	16/4/2017 11:16	57
14/4/2017 16:06	60	15/4/2017 9:11	59	15/4/2017 18:16	59	16/4/2017 11:21	59
14/4/2017 16:11	60	15/4/2017 9:16	59	15/4/2017 18:21	58	16/4/2017 11:26	58
14/4/2017 16:16	55	15/4/2017 9:21	60	15/4/2017 18:26	60	16/4/2017 11:31	59
14/4/2017 16:21	61	15/4/2017 9:26	58	15/4/2017 18:31	59	16/4/2017 11:36	58
14/4/2017 16:26	60	15/4/2017 9:31	59	15/4/2017 18:36	59	16/4/2017 11:41	62
14/4/2017 16:31	59	15/4/2017 9:36	60	15/4/2017 18:41	59	16/4/2017 11:46	59
14/4/2017 16:36	59	15/4/2017 9:41	59	15/4/2017 18:46	59	16/4/2017 11:51	58
14/4/2017 16:41	60	15/4/2017 9:46	59	15/4/2017 18:51	59	16/4/2017 11:56	58
14/4/2017 16:46	59	15/4/2017 9:51	60	15/4/2017 18:56	59	16/4/2017 12:01	57
14/4/2017 16:51	59	15/4/2017 9:56	60	15/4/2017 19:01	48	16/4/2017 12:06	58
14/4/2017 16:56	60	15/4/2017 10:01	59	15/4/2017 19:06	59	16/4/2017 12:11	59
14/4/2017 17:01	59	15/4/2017 10:06	59	15/4/2017 19:11	60	16/4/2017 12:16	58
14/4/2017 17:06	59	15/4/2017 10:11	59	15/4/2017 19:16	59	16/4/2017 12:21	61
14/4/2017 17:11	59	15/4/2017 10:16	59	15/4/2017 19:21	59	16/4/2017 12:26	58
14/4/2017 17:16	59	15/4/2017 10:21	59	15/4/2017 19:26	58	16/4/2017 12:31	58
14/4/2017 17:21	59	15/4/2017 10:26	60	15/4/2017 19:31	59	16/4/2017 12:36	58
14/4/2017 17:26	60	15/4/2017 10:31	60	15/4/2017 19:36	58	16/4/2017 12:41	61
14/4/2017 17:31	60	15/4/2017 10:36	60	15/4/2017 19:41	58	16/4/2017 12:46	60
14/4/2017 17:36	60	15/4/2017 10:41	59	15/4/2017 19:46	59	16/4/2017 12:51	58
14/4/2017 17:41	60	15/4/2017 10:46	59	15/4/2017 19:51	59	16/4/2017 12:56	58
14/4/2017 17:46	59	15/4/2017 10:51	59	15/4/2017 19:56	59	16/4/2017 13:01	59
14/4/2017 17:51	59	15/4/2017 10:56	60	15/4/2017 20:01	61	16/4/2017 13:06	60
14/4/2017 17:56	59	15/4/2017 11:01	58	15/4/2017 20:06	51	16/4/2017 13:11	58
14/4/2017 18:01	60	15/4/2017 11:06	59	15/4/2017 20:11	61	16/4/2017 13:16	59
14/4/2017 18:06	59	15/4/2017 11:11	61	15/4/2017 20:16	62	16/4/2017 13:21	61
14/4/2017 18:11	59	15/4/2017 11:16	61	15/4/2017 20:21	60	16/4/2017 13:26	58
14/4/2017 18:16	59	15/4/2017 11:21	58	15/4/2017 20:26	60	16/4/2017 13:31	58
14/4/2017 18:21	59	15/4/2017 11:26	60	15/4/2017 20:31	60	16/4/2017 13:36	57
14/4/2017 18:26	61	15/4/2017 11:31	60	15/4/2017 20:36	61	16/4/2017 13:41	57
14/4/2017 18:31	60	15/4/2017 11:36	60	15/4/2017 20:41	60	16/4/2017 13:46	59
14/4/2017 18:36	60	15/4/2017 11:41	61	15/4/2017 20:46	60	16/4/2017 13:51	58
14/4/2017 18:41	60	15/4/2017 11:46	61	15/4/2017 20:51	57	16/4/2017 13:56	57
14/4/2017 18:46	59	15/4/2017 11:51	60	15/4/2017 20:56	58	16/4/2017 14:01	58
14/4/2017 18:51	61	15/4/2017 11:56	61	15/4/2017 21:01	58	16/4/2017 14:06	57
14/4/2017 18:56	59	15/4/2017 12:01	62	15/4/2017 21:06	60	16/4/2017 14:11	58
14/4/2017 19:01	61	15/4/2017 12:06	61	15/4/2017 21:11	59	16/4/2017 14:16	58
14/4/2017 19:06	58	15/4/2017 12:11	60	15/4/2017 21:16	60	16/4/2017 14:21	58
14/4/2017 19:11	58	15/4/2017 12:16	61	15/4/2017 21:21	61	16/4/2017 14:26	59
14/4/2017 19:16	59	15/4/2017 12:21	61	15/4/2017 21:26	58	16/4/2017 14:31	58
14/4/2017 19:21	58	15/4/2017 12:26	61	15/4/2017 21:31	57	16/4/2017 14:36	58
14/4/2017 19:26	59	15/4/2017 12:31	60	15/4/2017 21:36	58	16/4/2017 14:41	57
14/4/2017 19:31	59	15/4/2017 12:36	60	15/4/2017 21:41	56	16/4/2017 14:46	57
14/4/2017 19:36	58	15/4/2017 12:41	57	15/4/2017 21:46	56	16/4/2017 14:51	57
14/4/2017 19:41	62	15/4/2017 12:46	60	15/4/2017 21:51	57	16/4/2017 14:56	57
14/4/2017 19:46	60	15/4/2017 12:51	60	15/4/2017 21:56	57	16/4/2017 15:01	59
14/4/2017 19:51	58	15/4/2017 12:56	61	15/4/2017 22:01	58	16/4/2017 15:06	58
14/4/2017 19:56	59	15/4/2017 13:01	60	15/4/2017 22:06	56	16/4/2017 15:11	57
14/4/2017 20:01	58	15/4/2017 13:06	60	15/4/2017 22:11	58	16/4/2017 15:16	59
14/4/2017 20:06	59	15/4/2017 13:11	60	15/4/2017 22:16	56	16/4/2017 15:21	58
14/4/2017 20:11	60	15/4/2017 13:16	61	15/4/2017 22:21	56	16/4/2017 15:26	59
14/4/2017 20:16	58	15/4/2017 13:21	62	15/4/2017 22:26	58	16/4/2017 15:31	59
14/4/2017 20:21	59	15/4/2017 13:26	61	15/4/2017 22:31	59	16/4/2017 15:36	57
14/4/2017 20:26	60	15/4/2017 13:31	61	15/4/2017 22:36	56	16/4/2017 15:41	57
14/4/2017 20:31	62	15/4/2017 13:36	61	15/4/2017 22:41	58	16/4/2017 15:46	58
14/4/2017 20:36	59	15/4/2017 13:41	61	15/4/2017 22:46	58	16/4/2017 15:51	56
14/4/2017 20:41	59	15/4/2017 13:46	61	15/4/2017 22:51	59	16/4/2017 15:56	57
14/4/2017 20:46	58	15/4/2017 13:51	59	15/4/2017 22:56	56	16/4/2017 16:01	56
14/4/2017 20:51	60	15/4/2017 13:56	61	16/4/2017 7:01	55	16/4/2017 16:06	57
14/4/2017 20:56	61	15/4/2017 14:01	59	16/4/2017 7:06	55	16/4/2017 16:11	61
14/4/2017 21:01	58	15/4/2017 14:06	59	16/4/2017 7:11	54	16/4/2017 16:16	56
14/4/2017 21:06	57	15/4/2017 14:11	59	16/4/2017 7:16	54	16/4/2017 16:21	57
14/4/2017 21:11	58	15/4/2017 14:16	59	16/4/2017 7:21	56	16/4/2017 16:26	56
14/4/2017 21:16	59	15/4/2017 14:21	59	16/4/2017 7:26	54	16/4/2017 16:31	56
14/4/2017 21:21	58	15/4/2017 14:26	59	16/4/2017 7:31	57	16/4/2017 16:36	58
14/4/2017 21:26	58	15/4/2017 14:31	59	16/4/2017 7:36	56	16/4/2017 16:41	57
14/4/2017 21:31	60	15/4/2017 14:36	60	16/4/2017 7:41	56	16/4/2017 16:46	56
14/4/2017 21:36	55	15/4/2017 14:41	59	16/4/2017 7:46	55	16/4/2017 16:51	57
14/4/2017 21:41	57	15/4/2017 14:46	59	16/4/2017 7:51	56	16/4/2017 16:56	57
14/4/2017 21:46	58	15/4/2017 14:51	59	16/4/2017 7:56	56	16/4/2017 17:01	57
14/4/2017 21:51	58	15/4/2017 14:56	59	16/4/2017 8:01	59	16/4/2017 17:06	57
14/4/2017 21:56	47	15/4/2017 15:01	59	16/4/2017 8:06	58	16/4/2017 17:11	57
14/4/2017 22:01	58	15/4/2017 15:06	59	16/4/2017 8:11	56	16/4/2017 17:16	57
14/4/2017 22:06	58	15/4/2017 15:11	58	16/4/2017 8:16	56	16/4/2017 17:21	58
14/4/2017 22:11	56	15/4/2017 15:16	60	16/4/2017 8:21	57	16/4/2017 17:26	56
14/4/2017 22:16	58	15/4/2017 15:21	59	16/4/2017 8:26	56	16/4/2017 17:31	58
14/4/2017 22:21	61	15/4/2017 15:26	59	16/4/2017 8:31	57	16/4/2017 17:36	57
14/4/2017 22:26	59	15/4/2017 15:31	58	16/4/2017 8:36	56	16/4/2017 17:41	57
14/4/2017 22:31	58	15/4/2017 15:36	59	16/4/2017 8:41	56	16/4/2017 17:46	58
14/4/2017 22:36	58	15/4/2017 15:41	59	16/4/2017 8:46	57	16/4/2017 17:51	57
14/4/2017 22:41	58	15/4/2017 15:46	59	16/4/2017 8:51	58	16/4/2017 17:56	58
14/4/2017 22:46	59	15/4/2017 15:51	59	16/4/2017 8:56	58	16/4/2017 18:01	59
14/4/2017 22:51	59	15/4/2017 15:56	59	16/4/2017 9:01	56	16/4/2017 18:06	59
14/4/2017 22:56	59	15/4/2017 16:01	59	16/4/2017 9:06	59	16/4/2017 18:11	60
15/4/2017 7:01	57	15/4/2017 16:06	58	16/4/2017 9:11	57	16/4/2017 18:16	60
15/4/2017 7:06	57	15/4/2017 16:11	58	16/4/2017 9:16	58	16/4/2017 18:21	57
15/4/2017 7:11	62	15/4/2017 16:16	58	16/4/2017 9:21	57	16/4/2017 18:26	58
15/4/2017 7:16	57	15/4/2017 16:21	60	16/4/2017 9:26	57	16/4/2017 18:31	57
15/4/2017 7:21	62	15/4/2017 16:26	58	16/4/2017 9:31	57	16/4/2017 18:36	58
15/4/2017 7:26	57	15/4/2017 16:31	58	16/4/2017 9:36	58	16/4/2017 18:41	59
15/4/2017 7:31	58	15/4/2017 16:36	58	16/4/2017 9:41	58	16/4/2017 18:46	59
15/4/2017 7:36	58	15/4/2017 16:41	58	16/4/2017 9:46	56	16/4/2017 18:51	57
15/4/2017 7:41	57	15/4/2017 16:46	59	16/4/2017 9:51	58	16/4/2017 18:56	60
15/4/2017 7:46	57	15/4/2017 16:51	59	16/4/2017 9:56	58	16/4/2017 19:01	58
15/4/2017 7:51	58	15/4/2017 16:56	58	16/4/2017 10:01	57	16/4/2017 19:06	58
15/4/2017 7:56	57	15/4/2017 17:01	59	16/4/2017 10:06	57	16/4/2017 19:11	58
15/4/2017 8:01	59	15/4/2017 17:06	59	16/4/2017 10:11	58	16/4/2017 19:16	60
15/4/2017 8:06	60	15/4/2017 17:11	60	16/4/2017 10:16	58	16/4/2017 19:21	57
15/4/2017 8:11	58	15/4/2017 17:16	59	16/4/2017 10:21	57	16/4/2017 19:26	58
15/4/2017 8:16	59	15/4/2017 17:21	58	16/4/2017 10:26	58	16/4/2017 19:31	58
15/4/2017 8:21	58	15/4/2017 17:26	59	16/4/2017 10:31	58	16/4/2017 19:36	59
15/4/2017 8:26	59	15/4/2017 17:31	60	16/4/2017 10:36	59	16/4/2017 19:41	59
15/4/2017 8:31	58	15/4/2017 17:36	59	16/4/2017 10:41	58	16/4/2017 19:46	59
15/4/2017 8:36	58	15/4/2017 17:41	60	16/4/2017 10:46	58	16/4/2017 19:51	60
15/4/2017 8:41	58	15/4/2017 17:46	61	16/4/2017 10:51	58	16/4/2017 19:56	58
15/4/2017 8:46	59	15/4/2017 17:51	59	16/4/2017 10:56	59	16/4/2017 20:01	58
15/4/2017 8:51	58	15/4/2017 17:56	61	16/4/2017 11:01	56	16/4/2017 20:06	58
15/4/2017 8:56	59	15/4/2017 18:01	59	16/4/2017 11:06	58	16/4/2017 20:11	59
						16	

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
17/4/2017 22:26	56	20/4/2017 19:31	58	22/4/2017 20:36	58	23/4/2017 13:41	58	23/4/2017 22:46	55	26/4/2017 19:51	62
17/4/2017 22:31	56	20/4/2017 19:36	58	22/4/2017 20:41	58	23/4/2017 13:46	58	23/4/2017 22:51	55	26/4/2017 19:56	57
17/4/2017 22:36	57	20/4/2017 19:41	61	22/4/2017 20:46	59	23/4/2017 13:51	61	23/4/2017 22:56	56	26/4/2017 20:01	58
17/4/2017 22:41	56	20/4/2017 19:46	58	22/4/2017 20:51	58	23/4/2017 13:56	59	24/4/2017 19:01	58	26/4/2017 20:06	57
17/4/2017 22:46	57	20/4/2017 19:51	57	22/4/2017 20:56	59	23/4/2017 14:01	58	24/4/2017 19:06	58	26/4/2017 20:11	58
17/4/2017 22:51	56	20/4/2017 19:56	57	22/4/2017 21:01	57	23/4/2017 14:06	57	24/4/2017 19:11	57	26/4/2017 20:16	58
17/4/2017 22:56	56	20/4/2017 20:01	57	22/4/2017 21:06	58	23/4/2017 14:11	57	24/4/2017 19:16	58	26/4/2017 20:21	58
18/4/2017 19:01	58	20/4/2017 20:06	57	22/4/2017 21:11	60	23/4/2017 14:16	58	24/4/2017 19:21	57	26/4/2017 20:26	57
18/4/2017 19:06	57	20/4/2017 20:11	57	22/4/2017 21:16	56	23/4/2017 14:21	58	24/4/2017 19:26	58	26/4/2017 20:31	59
18/4/2017 19:11	58	20/4/2017 20:16	58	22/4/2017 21:21	58	23/4/2017 14:26	61	24/4/2017 19:31	58	26/4/2017 20:36	61
18/4/2017 19:16	57	20/4/2017 20:21	57	22/4/2017 21:26	56	23/4/2017 14:31	59	24/4/2017 19:36	59	26/4/2017 20:41	58
18/4/2017 19:21	58	20/4/2017 20:26	57	22/4/2017 21:31	57	23/4/2017 14:36	59	24/4/2017 19:41	59	26/4/2017 20:46	58
18/4/2017 19:26	58	20/4/2017 20:31	57	22/4/2017 21:36	60	23/4/2017 14:41	54	24/4/2017 19:46	58	26/4/2017 20:51	58
18/4/2017 19:31	58	20/4/2017 20:36	57	22/4/2017 21:41	57	23/4/2017 14:46	60	24/4/2017 19:51	61	26/4/2017 20:56	58
18/4/2017 19:36	59	20/4/2017 20:41	56	22/4/2017 21:46	56	23/4/2017 14:51	58	24/4/2017 19:56	58	26/4/2017 21:01	60
18/4/2017 19:41	57	20/4/2017 20:46	57	22/4/2017 21:51	57	23/4/2017 14:56	61	24/4/2017 20:01	58	26/4/2017 21:06	59
18/4/2017 19:46	59	20/4/2017 20:51	57	22/4/2017 21:56	57	23/4/2017 15:01	57	24/4/2017 20:06	57	26/4/2017 21:11	61
18/4/2017 19:51	57	20/4/2017 20:56	57	22/4/2017 22:01	56	23/4/2017 15:06	58	24/4/2017 20:11	58	26/4/2017 21:16	58
18/4/2017 19:56	57	20/4/2017 21:01	56	22/4/2017 22:06	57	23/4/2017 15:11	58	24/4/2017 20:16	58	26/4/2017 21:21	58
18/4/2017 20:01	57	20/4/2017 21:06	56	22/4/2017 22:11	58	23/4/2017 15:16	60	24/4/2017 20:21	59	26/4/2017 21:26	58
18/4/2017 20:06	57	20/4/2017 21:11	57	22/4/2017 22:16	59	23/4/2017 15:21	58	24/4/2017 20:26	59	26/4/2017 21:31	58
18/4/2017 20:11	57	20/4/2017 21:16	56	22/4/2017 22:21	57	23/4/2017 15:26	60	24/4/2017 20:31	56	26/4/2017 21:36	59
18/4/2017 20:16	58	20/4/2017 21:21	57	22/4/2017 22:26	58	23/4/2017 15:31	61	24/4/2017 20:36	56	26/4/2017 21:41	61
18/4/2017 20:21	57	20/4/2017 21:26	56	22/4/2017 22:31	56	23/4/2017 15:36	58	24/4/2017 20:41	59	26/4/2017 21:46	58
18/4/2017 20:26	57	20/4/2017 21:31	56	22/4/2017 22:36	57	23/4/2017 15:41	59	24/4/2017 20:46	57	26/4/2017 21:51	57
18/4/2017 20:31	57	20/4/2017 21:36	56	22/4/2017 22:41	57	23/4/2017 15:46	58	24/4/2017 20:51	58	26/4/2017 21:56	59
18/4/2017 20:36	58	20/4/2017 21:41	56	22/4/2017 22:46	56	23/4/2017 15:51	58	24/4/2017 20:56	57	26/4/2017 22:01	59
18/4/2017 20:41	59	20/4/2017 21:46	56	22/4/2017 22:51	57	23/4/2017 15:56	57	24/4/2017 21:01	56	26/4/2017 22:06	61
18/4/2017 20:46	57	20/4/2017 21:51	57	22/4/2017 22:56	58	23/4/2017 16:01	58	24/4/2017 21:06	56	26/4/2017 22:11	62
18/4/2017 20:51	57	20/4/2017 21:56	57	23/4/2017 7:01	55	23/4/2017 16:06	56	24/4/2017 21:11	55	26/4/2017 22:16	57
18/4/2017 20:56	57	20/4/2017 22:01	57	23/4/2017 7:06	54	23/4/2017 16:11	57	24/4/2017 21:16	58	26/4/2017 22:21	58
18/4/2017 21:01	58	20/4/2017 22:06	58	23/4/2017 7:11	54	23/4/2017 16:16	59	24/4/2017 21:21	60	26/4/2017 22:26	58
18/4/2017 21:06	57	20/4/2017 22:11	57	23/4/2017 7:16	55	23/4/2017 16:21	59	24/4/2017 21:26	57	26/4/2017 22:31	59
18/4/2017 21:11	57	20/4/2017 22:16	57	23/4/2017 7:21	56	23/4/2017 16:26	57	24/4/2017 21:31	57	26/4/2017 22:36	58
18/4/2017 21:16	59	20/4/2017 22:21	57	23/4/2017 7:26	55	23/4/2017 16:31	60	24/4/2017 21:36	60	26/4/2017 22:41	56
18/4/2017 21:21	60	20/4/2017 22:26	57	23/4/2017 7:31	54	23/4/2017 16:36	58	24/4/2017 21:41	56	26/4/2017 22:46	56
18/4/2017 21:26	58	20/4/2017 22:31	57	23/4/2017 7:36	55	23/4/2017 16:41	57	24/4/2017 21:46	57	26/4/2017 22:51	57
18/4/2017 21:31	58	20/4/2017 22:36	57	23/4/2017 7:41	56	23/4/2017 16:46	58	24/4/2017 21:51	60	26/4/2017 22:56	56
18/4/2017 21:36	57	20/4/2017 22:41	57	23/4/2017 7:46	55	23/4/2017 16:51	58	24/4/2017 21:56	57		
18/4/2017 21:41	57	20/4/2017 22:46	57	23/4/2017 7:51	56	23/4/2017 16:56	60	24/4/2017 22:01	58	Night time: 23:00-07:00	
18/4/2017 21:46	56	20/4/2017 22:51	57	23/4/2017 7:56	56	23/4/2017 17:01	57	24/4/2017 22:06	57		
18/4/2017 21:51	57	20/4/2017 22:56	57	23/4/2017 8:01	56	23/4/2017 17:06	57	24/4/2017 22:11	57	27/3/2017 0:01	55
18/4/2017 21:56	57	21/4/2017 19:01	58	23/4/2017 8:06	55	23/4/2017 17:11	58	24/4/2017 22:16	57	27/3/2017 0:06	55
18/4/2017 22:01	58	21/4/2017 19:06	57	23/4/2017 8:11	57	23/4/2017 17:16	57	24/4/2017 22:21	57	27/3/2017 0:11	55
18/4/2017 22:06	58	21/4/2017 19:11	58	23/4/2017 8:16	57	23/4/2017 17:21	60	24/4/2017 22:26	57	27/3/2017 0:16	57
18/4/2017 22:11	56	21/4/2017 19:16	59	23/4/2017 8:21	58	23/4/2017 17:26	58	24/4/2017 22:31	56	27/3/2017 0:21	57
18/4/2017 22:16	56	21/4/2017 19:21	59	23/4/2017 8:26	56	23/4/2017 17:31	58	24/4/2017 22:36	56	27/3/2017 0:26	55
18/4/2017 22:21	59	21/4/2017 19:26	59	23/4/2017 8:31	59	23/4/2017 17:36	59	24/4/2017 22:41	56	27/3/2017 0:31	55
18/4/2017 22:26	58	21/4/2017 19:31	59	23/4/2017 8:36	56	23/4/2017 17:41	57	24/4/2017 22:46	56	27/3/2017 0:36	54
18/4/2017 22:31	57	21/4/2017 19:36	58	23/4/2017 8:41	56	23/4/2017 17:46	57	24/4/2017 22:51	56	27/3/2017 0:41	55
18/4/2017 22:36	57	21/4/2017 19:41	58	23/4/2017 8:46	56	23/4/2017 17:51	56	24/4/2017 22:56	58	27/3/2017 0:46	54
18/4/2017 22:41	57	21/4/2017 19:46	58	23/4/2017 8:51	57	23/4/2017 17:56	57	25/4/2017 19:01	57	27/3/2017 0:51	54
18/4/2017 22:46	60	21/4/2017 19:51	59	23/4/2017 8:56	56	23/4/2017 18:01	57	25/4/2017 19:06	58	27/3/2017 0:56	54
18/4/2017 22:51	58	21/4/2017 19:56	59	23/4/2017 9:01	57	23/4/2017 18:06	59	25/4/2017 19:11	57	27/3/2017 1:01	54
18/4/2017 22:56	60	21/4/2017 20:01	58	23/4/2017 9:06	55	23/4/2017 18:11	57	25/4/2017 19:16	60	27/3/2017 1:06	53
19/4/2017 19:01	59	21/4/2017 20:06	58	23/4/2017 9:11	59	23/4/2017 18:16	59	25/4/2017 19:21	59	27/3/2017 1:11	53
19/4/2017 19:06	58	21/4/2017 20:11	58	23/4/2017 9:16	56	23/4/2017 18:21	59	25/4/2017 19:26	57	27/3/2017 1:16	54
19/4/2017 19:11	59	21/4/2017 20:16	58	23/4/2017 9:21	59	23/4/2017 18:26	58	25/4/2017 19:31	58	27/3/2017 1:21	54
19/4/2017 19:16	58	21/4/2017 20:21	57	23/4/2017 9:26	57	23/4/2017 18:31	56	25/4/2017 19:36	59	27/3/2017 1:26	53
19/4/2017 19:21	58	21/4/2017 20:26	58	23/4/2017 9:31	58	23/4/2017 18:36	57	25/4/2017 19:41	58	27/3/2017 1:31	53
19/4/2017 19:26	58	21/4/2017 20:31	57	23/4/2017 9:36	59	23/4/2017 18:41	58	25/4/2017 19:46	58	27/3/2017 1:36	53
19/4/2017 19:31	58	21/4/2017 20:36	58	23/4/2017 9:41	57	23/4/2017 18:46	58	25/4/2017 19:51	58	27/3/2017 1:41	53
19/4/2017 19:36	58	21/4/2017 20:41	57	23/4/2017 9:46	58	23/4/2017 18:51	57	25/4/2017 19:56	57	27/3/2017 1:46	53
19/4/2017 19:41	59	21/4/2017 20:46	57	23/4/2017 9:51	57	23/4/2017 18:56	58	25/4/2017 20:01	59	27/3/2017 1:51	53
19/4/2017 19:46	57	21/4/2017 20:51	57	23/4/2017 9:56	58	23/4/2017 19:01	59	25/4/2017 20:06	57	27/3/2017 1:56	53
19/4/2017 19:51	57	21/4/2017 20:56	57	23/4/2017 10:01	58	23/4/2017 19:06	52	25/4/2017 20:11	60	27/3/2017 2:01	53
19/4/2017 19:56	57	21/4/2017 21:01	57	23/4/2017 10:06	58	23/4/2017 19:11	56	25/4/2017 20:16	59	27/3/2017 2:06	54
19/4/2017 20:01	57	21/4/2017 21:06	57	23/4/2017 10:11	57	23/4/2017 19:16	58	25/4/2017 20:21	57	27/3/2017 2:11	54
19/4/2017 20:06	57	21/4/2017 21:11	57	23/4/2017 10:16	56	23/4/2017 19:21	56	25/4/2017 20:26	57	27/3/2017 2:16	53
19/4/2017 20:11	58	21/4/2017 21:16	60	23/4/2017 10:21	58	23/4/2017 19:26	58	25/4/2017 20:31	59	27/3/2017 2:21	53
19/4/2017 20:16	58	21/4/2017 21:21	57	23/4/2017 10:26	57	23/4/2017 19:31	59	25/4/2017 20:36	57	27/3/2017 2:26	53
19/4/2017 20:21	58	21/4/2017 21:26	57	23/4/2017 10:31	61	23/4/2017 19:36	56	25/4/2017 20:41	59	27/3/2017 2:31	56
19/4/2017 20:26	58	21/4/2017 21:31	58	23/4/2017 10:36	59	23/4/2017 19:41	57	25/4/2017 20:46	57	27/3/2017 2:36	55
19/4/2017 20:31	58	21/4/2017 21:36	57	23/4/2017 10:41	57	23/4/2017 19:46	59				

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)											
27/3/2017 5:41	52	28/3/2017 6:46	57	29/3/2017 23:51	54	31/3/2017 0:56	53	1/4/2017 2:01	54	2/4/2017 3:06	54		
27/3/2017 5:46	53	28/3/2017 6:51	56	29/3/2017 23:56	55	31/3/2017 1:01	53	1/4/2017 2:06	54	2/4/2017 3:11	54		
27/3/2017 5:51	52	28/3/2017 6:56	56	30/3/2017 0:01	55	31/3/2017 1:06	54	1/4/2017 2:11	53	2/4/2017 3:16	53		
27/3/2017 5:56	52	28/3/2017 23:01	57	30/3/2017 0:06	54	31/3/2017 1:11	53	1/4/2017 2:16	53	2/4/2017 3:21	54		
27/3/2017 6:01	53	28/3/2017 23:06	57	30/3/2017 0:11	54	31/3/2017 1:16	53	1/4/2017 2:21	54	2/4/2017 3:26	53		
27/3/2017 6:06	54	28/3/2017 23:11	56	30/3/2017 0:16	55	31/3/2017 1:21	53	1/4/2017 2:26	53	2/4/2017 3:31	53		
27/3/2017 6:11	53	28/3/2017 23:16	55	30/3/2017 0:21	55	31/3/2017 1:26	53	1/4/2017 2:31	54	2/4/2017 3:36	53		
27/3/2017 6:16	54	28/3/2017 23:21	55	30/3/2017 0:26	56	31/3/2017 1:31	53	1/4/2017 2:36	55	2/4/2017 3:41	52		
27/3/2017 6:21	56	28/3/2017 23:26	55	30/3/2017 0:31	56	31/3/2017 1:36	54	1/4/2017 2:41	54	2/4/2017 3:46	53		
27/3/2017 6:26	54	28/3/2017 23:31	55	30/3/2017 0:36	54	31/3/2017 1:41	52	1/4/2017 2:46	54	2/4/2017 3:51	53		
27/3/2017 6:31	54	28/3/2017 23:36	55	30/3/2017 0:41	54	31/3/2017 1:46	54	1/4/2017 2:51	53	2/4/2017 3:56	53		
27/3/2017 6:36	57	28/3/2017 23:41	55	30/3/2017 0:46	54	31/3/2017 1:51	53	1/4/2017 2:56	53	2/4/2017 4:01	53		
27/3/2017 6:41	57	28/3/2017 23:46	55	30/3/2017 0:51	54	31/3/2017 1:56	54	1/4/2017 3:01	53	2/4/2017 4:06	53		
27/3/2017 6:46	56	28/3/2017 23:51	55	30/3/2017 0:56	55	31/3/2017 2:01	53	1/4/2017 3:06	53	2/4/2017 4:11	52		
27/3/2017 6:51	56	28/3/2017 23:56	56	30/3/2017 1:01	53	31/3/2017 2:06	52	1/4/2017 3:11	53	2/4/2017 4:16	53		
27/3/2017 6:56	55	29/3/2017 0:01	54	30/3/2017 1:06	53	31/3/2017 2:11	52	1/4/2017 3:16	53	2/4/2017 4:21	53		
27/3/2017 23:01	56	29/3/2017 0:06	55	30/3/2017 1:11	53	31/3/2017 2:16	52	1/4/2017 3:21	53	2/4/2017 4:26	53		
27/3/2017 23:06	56	29/3/2017 0:11	56	30/3/2017 1:16	53	31/3/2017 2:21	52	1/4/2017 3:26	53	2/4/2017 4:31	52		
27/3/2017 23:11	55	29/3/2017 0:16	55	30/3/2017 1:21	54	31/3/2017 2:26	52	1/4/2017 3:31	54	2/4/2017 4:36	52		
27/3/2017 23:16	55	29/3/2017 0:21	54	30/3/2017 1:26	53	31/3/2017 2:31	54	1/4/2017 3:36	52	2/4/2017 4:41	51		
27/3/2017 23:21	55	29/3/2017 0:26	54	30/3/2017 1:31	52	31/3/2017 2:36	53	1/4/2017 3:41	53	2/4/2017 4:46	52		
27/3/2017 23:26	55	29/3/2017 0:31	54	30/3/2017 1:36	52	31/3/2017 2:41	53	1/4/2017 3:46	53	2/4/2017 4:51	53		
27/3/2017 23:31	55	29/3/2017 0:36	55	30/3/2017 1:41	53	31/3/2017 2:46	53	1/4/2017 3:51	53	2/4/2017 4:56	52		
27/3/2017 23:36	55	29/3/2017 0:41	55	30/3/2017 1:46	52	31/3/2017 2:51	52	1/4/2017 3:56	52	2/4/2017 5:01	52		
27/3/2017 23:41	56	29/3/2017 0:46	54	30/3/2017 1:51	53	31/3/2017 2:56	52	1/4/2017 4:01	53	2/4/2017 5:06	53		
27/3/2017 23:46	55	29/3/2017 0:51	53	30/3/2017 1:56	55	31/3/2017 3:01	51	1/4/2017 4:06	53	2/4/2017 5:11	52		
27/3/2017 23:51	56	29/3/2017 0:56	53	30/3/2017 2:01	52	31/3/2017 3:06	51	1/4/2017 4:11	53	2/4/2017 5:16	52		
27/3/2017 23:56	55	29/3/2017 1:01	54	30/3/2017 2:06	52	31/3/2017 3:11	52	1/4/2017 4:16	52	2/4/2017 5:21	52		
28/3/2017 0:01	55	29/3/2017 1:06	53	30/3/2017 2:11	52	31/3/2017 3:16	52	1/4/2017 4:21	53	2/4/2017 5:26	53		
28/3/2017 0:06	54	29/3/2017 1:11	53	30/3/2017 2:16	52	31/3/2017 3:21	52	1/4/2017 4:26	53	2/4/2017 5:31	52		
28/3/2017 0:11	55	29/3/2017 1:16	54	30/3/2017 2:21	51	31/3/2017 3:26	51	1/4/2017 4:31	54	2/4/2017 5:36	52		
28/3/2017 0:16	55	29/3/2017 1:21	53	30/3/2017 2:26	52	31/3/2017 3:31	51	1/4/2017 4:36	54	2/4/2017 5:41	53		
28/3/2017 0:21	55	29/3/2017 1:26	54	30/3/2017 2:31	52	31/3/2017 3:36	51	1/4/2017 4:41	52	2/4/2017 5:46	53		
28/3/2017 0:26	54	29/3/2017 1:31	53	30/3/2017 2:36	52	31/3/2017 3:41	52	1/4/2017 4:46	53	2/4/2017 5:51	53		
28/3/2017 0:31	54	29/3/2017 1:36	53	30/3/2017 2:41	52	31/3/2017 3:46	51	1/4/2017 4:51	53	2/4/2017 5:56	52		
28/3/2017 0:36	54	29/3/2017 1:41	52	30/3/2017 2:46	53	31/3/2017 3:51	52	1/4/2017 4:56	52	2/4/2017 6:01	52		
28/3/2017 0:41	54	29/3/2017 1:46	53	30/3/2017 2:51	51	31/3/2017 3:56	51	1/4/2017 5:01	53	2/4/2017 6:06	53		
28/3/2017 0:46	54	29/3/2017 1:51	52	30/3/2017 2:56	52	31/3/2017 4:01	51	1/4/2017 5:06	53	2/4/2017 6:11	53		
28/3/2017 0:51	54	29/3/2017 1:56	54	30/3/2017 3:01	51	31/3/2017 4:06	51	1/4/2017 5:11	53	2/4/2017 6:16	55		
28/3/2017 0:56	54	29/3/2017 2:01	52	30/3/2017 3:06	51	31/3/2017 4:11	51	1/4/2017 5:16	55	2/4/2017 6:21	54		
28/3/2017 1:01	54	29/3/2017 2:06	52	30/3/2017 3:11	51	31/3/2017 4:16	52	1/4/2017 5:21	55	2/4/2017 6:26	54		
28/3/2017 1:06	54	29/3/2017 2:11	52	30/3/2017 3:16	52	31/3/2017 4:21	52	1/4/2017 5:26	52	2/4/2017 6:31	56		
28/3/2017 1:11	54	29/3/2017 2:16	52	30/3/2017 3:21	51	31/3/2017 4:26	51	1/4/2017 5:31	53	2/4/2017 6:36	55		
28/3/2017 1:16	54	29/3/2017 2:21	54	30/3/2017 3:26	52	31/3/2017 4:31	51	1/4/2017 5:36	52	2/4/2017 6:41	55		
28/3/2017 1:21	53	29/3/2017 2:26	51	30/3/2017 3:31	55	31/3/2017 4:36	52	1/4/2017 5:41	53	2/4/2017 6:46	55		
28/3/2017 1:26	54	29/3/2017 2:31	52	30/3/2017 3:36	52	31/3/2017 4:41	51	1/4/2017 5:46	53	2/4/2017 6:51	55		
28/3/2017 1:31	57	29/3/2017 2:36	52	30/3/2017 3:41	52	31/3/2017 4:46	52	1/4/2017 5:51	53	2/4/2017 6:56	54		
28/3/2017 1:36	55	29/3/2017 2:41	53	30/3/2017 3:46	51	31/3/2017 4:51	52	1/4/2017 5:56	52	2/4/2017 23:01	55		
28/3/2017 1:41	54	29/3/2017 2:46	52	30/3/2017 3:51	52	31/3/2017 4:56	51	1/4/2017 6:01	52	2/4/2017 23:06	55		
28/3/2017 1:46	54	29/3/2017 2:51	53	30/3/2017 3:56	51	31/3/2017 5:01	53	1/4/2017 6:06	53	2/4/2017 23:11	57		
28/3/2017 1:51	54	29/3/2017 2:56	52	30/3/2017 4:01	53	31/3/2017 5:06	52	1/4/2017 6:11	54	2/4/2017 23:16	54		
28/3/2017 1:56	54	29/3/2017 3:01	51	30/3/2017 4:06	51	31/3/2017 5:11	51	1/4/2017 6:16	54	2/4/2017 23:21	56		
28/3/2017 2:01	54	29/3/2017 3:06	51	30/3/2017 4:11	51	31/3/2017 5:16	52	1/4/2017 6:21	54	2/4/2017 23:26	55		
28/3/2017 2:06	53	29/3/2017 3:11	51	30/3/2017 4:16	52	31/3/2017 5:21	52	1/4/2017 6:26	54	2/4/2017 23:31	57		
28/3/2017 2:11	54	29/3/2017 3:16	51	30/3/2017 4:21	51	31/3/2017 5:26	52	1/4/2017 6:31	55	2/4/2017 23:36	55		
28/3/2017 2:16	53	29/3/2017 3:21	52	30/3/2017 4:26	52	31/3/2017 5:31	52	1/4/2017 6:36	54	2/4/2017 23:41	55		
28/3/2017 2:21	53	29/3/2017 3:26	51	30/3/2017 4:31	50	31/3/2017 5:36	51	1/4/2017 6:41	54	2/4/2017 23:46	54		
28/3/2017 2:26	53	29/3/2017 3:31	51	30/3/2017 4:36	50	31/3/2017 5:41	52	1/4/2017 6:46	55	2/4/2017 23:51	53		
28/3/2017 2:31	54	29/3/2017 3:36	52	30/3/2017 4:41	51	31/3/2017 5:46	52	1/4/2017 6:51	56	2/4/2017 23:56	53		
28/3/2017 2:36	53	29/3/2017 3:41	51	30/3/2017 4:46	51	31/3/2017 5:51	52	1/4/2017 6:56	55	3/4/2017 0:01	53		
28/3/2017 2:41	53	29/3/2017 3:46	51	30/3/2017 4:51	52	31/3/2017 5:56	52	1/4/2017 23:01	57	3/4/2017 0:06	54		
28/3/2017 2:46	53	29/3/2017 3:51	54	30/3/2017 4:56	51	31/3/2017 6:01	53	1/4/2017 23:06	57	3/4/2017 0:11	53		
28/3/2017 2:51	53	29/3/2017 3:56	52	30/3/2017 5:01	53	31/3/2017 6:06	54	1/4/2017 23:11	55	3/4/2017 0:16	53		
28/3/2017 2:56	53	29/3/2017 4:01	51	30/3/2017 5:06	52	31/3/2017 6:11	54	1/4/2017 23:16	57	3/4/2017 0:21	54		
28/3/2017 3:01	53	29/3/2017 4:06	51	30/3/2017 5:11	57	31/3/2017 6:16	54	1/4/2017 23:21	55	3/4/2017 0:26	53		
28/3/2017 3:06	53	29/3/2017 4:11	52	30/3/2017 5:16	53	31/3/2017 6:21	54	1/4/2017 23:26	56	3/4/2017 0:31	53		
28/3/2017 3:11	54	29/3/2017 4:16	51	30/3/2017 5:21	52	31/3/2017 6:26	55	1/4/2017 23:31	56	3/4/2017 0:36	53		
28/3/2017 3:16	54	29/3/2017 4:21	53	30/3/2017 5:26	51	31/3/2017 6:31	54	1/4/2017 23:36	56	3/4/2017 0:41	53		
28/3/2017 3:21	53	29/3/2017 4:26	55	30/3/2017 5:31	52	31/3/2017 6:36	54	1/4/2017 23:41	56	3/4/2017 0:46	52		
28/3/2017 3:26	56	29/3/2017 4:31	52	30/3/2017 5:36	52	31/3/2017 6:41	55	1/4/2017 23:46	56	3/4/2017 0:51	52		
28/3/2017 3:31	53	29/3/2017 4:36	52	30/3/2017 5:41	52	31/3/2017 6:46	57	1/4/2017 23:51	55	3/4/2017 0:56	53		
28/3/2017 3:36	53	29/3/2017 4:41	51	30/3/2017 5:46	51	31/3/2017 6:51	56	1/4/2017 23:56	56	3/4/2017 1:01	52		
28/3/2017 3:41	55	29/3/2017 4:46	51	30/3/2017 5:51	52	31/3/2017 6:56	57						

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
3/4/2017 4:11	50	4/4/2017 5:16	53	5/4/2017 6:21	56	6/4/2017 23:26	55	8/4/2017 0:31	57	9/4/2017 1:36	55
3/4/2017 4:16	50	4/4/2017 5:21	52	5/4/2017 6:26	55	6/4/2017 23:31	55	8/4/2017 0:36	58	9/4/2017 1:41	55
3/4/2017 4:21	51	4/4/2017 5:26	53	5/4/2017 6:31	55	6/4/2017 23:36	55	8/4/2017 0:41	57	9/4/2017 1:46	55
3/4/2017 4:26	50	4/4/2017 5:31	53	5/4/2017 6:36	47	6/4/2017 23:41	54	8/4/2017 0:46	57	9/4/2017 1:51	55
3/4/2017 4:31	50	4/4/2017 5:36	52	5/4/2017 6:41	55	6/4/2017 23:46	55	8/4/2017 0:51	56	9/4/2017 1:56	54
3/4/2017 4:36	49	4/4/2017 5:41	53	5/4/2017 6:46	55	6/4/2017 23:51	54	8/4/2017 0:56	56	9/4/2017 2:01	54
3/4/2017 4:41	49	4/4/2017 5:46	55	5/4/2017 6:51	55	6/4/2017 23:56	54	8/4/2017 1:01	55	9/4/2017 2:06	54
3/4/2017 4:46	51	4/4/2017 5:51	52	5/4/2017 6:56	56	7/4/2017 0:01	55	8/4/2017 1:06	56	9/4/2017 2:11	54
3/4/2017 4:51	50	4/4/2017 5:56	54	5/4/2017 7:01	55	7/4/2017 0:06	55	8/4/2017 1:11	56	9/4/2017 2:16	54
3/4/2017 4:56	51	4/4/2017 6:01	53	5/4/2017 7:06	55	7/4/2017 0:11	56	8/4/2017 1:16	56	9/4/2017 2:21	54
3/4/2017 5:01	51	4/4/2017 6:06	53	5/4/2017 7:11	56	7/4/2017 0:16	58	8/4/2017 1:21	55	9/4/2017 2:26	53
3/4/2017 5:06	51	4/4/2017 6:11	54	5/4/2017 7:16	56	7/4/2017 0:21	54	8/4/2017 1:26	56	9/4/2017 2:31	54
3/4/2017 5:11	51	4/4/2017 6:16	55	5/4/2017 7:21	55	7/4/2017 0:26	54	8/4/2017 1:31	58	9/4/2017 2:36	54
3/4/2017 5:16	51	4/4/2017 6:21	53	5/4/2017 7:26	56	7/4/2017 0:31	55	8/4/2017 1:36	57	9/4/2017 2:41	54
3/4/2017 5:21	52	4/4/2017 6:26	54	5/4/2017 7:31	56	7/4/2017 0:36	55	8/4/2017 1:41	55	9/4/2017 2:46	54
3/4/2017 5:26	55	4/4/2017 6:31	54	5/4/2017 7:36	54	7/4/2017 0:41	54	8/4/2017 1:46	55	9/4/2017 2:51	54
3/4/2017 5:31	52	4/4/2017 6:36	54	5/4/2017 7:41	54	7/4/2017 0:46	53	8/4/2017 1:51	55	9/4/2017 2:56	54
3/4/2017 5:36	51	4/4/2017 6:41	53	5/4/2017 7:46	54	7/4/2017 0:51	54	8/4/2017 1:56	55	9/4/2017 3:01	54
3/4/2017 5:41	52	4/4/2017 6:46	55	5/4/2017 7:51	54	7/4/2017 0:56	55	8/4/2017 2:01	56	9/4/2017 3:06	54
3/4/2017 5:46	52	4/4/2017 6:51	57	5/4/2017 7:56	55	7/4/2017 1:01	53	8/4/2017 2:06	56	9/4/2017 3:11	54
3/4/2017 5:51	54	4/4/2017 6:56	56	6/4/2017 0:01	55	7/4/2017 1:06	53	8/4/2017 2:11	55	9/4/2017 3:16	55
3/4/2017 5:56	52	4/4/2017 7:01	55	6/4/2017 0:06	54	7/4/2017 1:11	53	8/4/2017 2:16	55	9/4/2017 3:21	54
3/4/2017 6:01	53	4/4/2017 7:06	54	6/4/2017 0:11	54	7/4/2017 1:16	54	8/4/2017 2:21	55	9/4/2017 3:26	54
3/4/2017 6:06	53	4/4/2017 7:11	54	6/4/2017 0:16	54	7/4/2017 1:21	54	8/4/2017 2:26	56	9/4/2017 3:31	54
3/4/2017 6:11	53	4/4/2017 7:16	56	6/4/2017 0:21	55	7/4/2017 1:26	53	8/4/2017 2:31	56	9/4/2017 3:36	55
3/4/2017 6:16	54	4/4/2017 7:21	55	6/4/2017 0:26	55	7/4/2017 1:31	53	8/4/2017 2:36	55	9/4/2017 3:41	53
3/4/2017 6:21	54	4/4/2017 7:26	54	6/4/2017 0:31	54	7/4/2017 1:36	53	8/4/2017 2:41	55	9/4/2017 3:46	53
3/4/2017 6:26	54	4/4/2017 7:31	54	6/4/2017 0:36	54	7/4/2017 1:41	53	8/4/2017 2:46	55	9/4/2017 3:51	54
3/4/2017 6:31	54	4/4/2017 7:36	55	6/4/2017 0:41	53	7/4/2017 1:46	52	8/4/2017 2:51	55	9/4/2017 3:56	54
3/4/2017 6:36	54	4/4/2017 7:41	54	6/4/2017 0:46	54	7/4/2017 1:51	53	8/4/2017 2:56	55	9/4/2017 4:01	54
3/4/2017 6:41	55	4/4/2017 7:46	54	6/4/2017 0:51	53	7/4/2017 1:56	53	8/4/2017 3:01	57	9/4/2017 4:06	54
3/4/2017 6:46	56	4/4/2017 7:51	54	6/4/2017 0:56	53	7/4/2017 2:01	52	8/4/2017 3:06	55	9/4/2017 4:11	54
3/4/2017 6:51	56	4/4/2017 7:56	54	6/4/2017 1:01	53	7/4/2017 2:06	52	8/4/2017 3:11	55	9/4/2017 4:16	54
3/4/2017 6:56	56	5/4/2017 0:01	56	6/4/2017 1:06	53	7/4/2017 2:11	52	8/4/2017 3:16	54	9/4/2017 4:21	54
3/4/2017 7:01	56	5/4/2017 0:06	55	6/4/2017 1:11	55	7/4/2017 2:16	53	8/4/2017 3:21	56	9/4/2017 4:26	54
3/4/2017 7:06	56	5/4/2017 0:11	55	6/4/2017 1:16	54	7/4/2017 2:21	52	8/4/2017 3:26	56	9/4/2017 4:31	53
3/4/2017 7:11	55	5/4/2017 0:16	54	6/4/2017 1:21	53	7/4/2017 2:26	52	8/4/2017 3:31	54	9/4/2017 4:36	53
3/4/2017 7:16	55	5/4/2017 0:21	56	6/4/2017 1:26	52	7/4/2017 2:31	52	8/4/2017 3:36	55	9/4/2017 4:41	54
3/4/2017 7:21	56	5/4/2017 0:26	55	6/4/2017 1:31	52	7/4/2017 2:36	53	8/4/2017 3:41	54	9/4/2017 4:46	55
3/4/2017 7:26	55	5/4/2017 0:31	55	6/4/2017 1:36	52	7/4/2017 2:41	52	8/4/2017 3:46	56	9/4/2017 4:51	55
3/4/2017 7:31	55	5/4/2017 0:36	54	6/4/2017 1:41	56	7/4/2017 2:46	52	8/4/2017 3:51	58	9/4/2017 4:56	54
3/4/2017 7:36	55	5/4/2017 0:41	54	6/4/2017 1:46	54	7/4/2017 2:51	54	8/4/2017 3:56	55	9/4/2017 5:01	53
3/4/2017 7:41	56	5/4/2017 0:46	54	6/4/2017 1:51	52	7/4/2017 2:56	53	8/4/2017 4:01	54	9/4/2017 5:06	56
3/4/2017 7:46	56	5/4/2017 0:51	53	6/4/2017 1:56	52	7/4/2017 3:01	52	8/4/2017 4:06	54	9/4/2017 5:11	54
3/4/2017 7:51	55	5/4/2017 0:56	53	6/4/2017 2:01	52	7/4/2017 3:06	55	8/4/2017 4:11	56	9/4/2017 5:16	54
3/4/2017 7:56	55	5/4/2017 1:01	54	6/4/2017 2:06	55	7/4/2017 3:11	52	8/4/2017 4:16	57	9/4/2017 5:21	54
4/4/2017 0:01	55	5/4/2017 1:06	53	6/4/2017 2:11	52	7/4/2017 3:16	52	8/4/2017 4:21	54	9/4/2017 5:26	54
4/4/2017 0:06	55	5/4/2017 1:11	54	6/4/2017 2:16	53	7/4/2017 3:21	52	8/4/2017 4:26	54	9/4/2017 5:31	55
4/4/2017 0:11	55	5/4/2017 1:16	53	6/4/2017 2:21	52	7/4/2017 3:26	52	8/4/2017 4:31	55	9/4/2017 5:36	55
4/4/2017 0:16	56	5/4/2017 1:21	54	6/4/2017 2:26	52	7/4/2017 3:31	51	8/4/2017 4:36	55	9/4/2017 5:41	54
4/4/2017 0:21	55	5/4/2017 1:26	52	6/4/2017 2:31	52	7/4/2017 3:36	51	8/4/2017 4:41	55	9/4/2017 5:46	54
4/4/2017 0:26	55	5/4/2017 1:31	53	6/4/2017 2:36	53	7/4/2017 3:41	51	8/4/2017 4:46	55	9/4/2017 5:51	55
4/4/2017 0:31	54	5/4/2017 1:36	52	6/4/2017 2:41	52	7/4/2017 3:46	53	8/4/2017 4:51	54	9/4/2017 5:56	56
4/4/2017 0:36	54	5/4/2017 1:41	52	6/4/2017 2:46	52	7/4/2017 3:51	54	8/4/2017 4:56	54	9/4/2017 6:01	56
4/4/2017 0:41	55	5/4/2017 1:46	53	6/4/2017 2:51	52	7/4/2017 3:56	54	8/4/2017 5:01	54	9/4/2017 6:06	55
4/4/2017 0:46	54	5/4/2017 1:51	54	6/4/2017 2:56	52	7/4/2017 4:01	56	8/4/2017 5:06	55	9/4/2017 6:11	55
4/4/2017 0:51	54	5/4/2017 1:56	52	6/4/2017 3:01	52	7/4/2017 4:06	51	8/4/2017 5:11	55	9/4/2017 6:16	56
4/4/2017 0:56	54	5/4/2017 2:01	53	6/4/2017 3:06	53	7/4/2017 4:11	51	8/4/2017 5:16	54	9/4/2017 6:21	55
4/4/2017 1:01	54	5/4/2017 2:06	52	6/4/2017 3:11	51	7/4/2017 4:16	52	8/4/2017 5:21	54	9/4/2017 6:26	55
4/4/2017 1:06	53	5/4/2017 2:11	53	6/4/2017 3:16	52	7/4/2017 4:21	52	8/4/2017 5:26	57	9/4/2017 6:31	56
4/4/2017 1:11	54	5/4/2017 2:16	54	6/4/2017 3:21	52	7/4/2017 4:26	51	8/4/2017 5:31	56	9/4/2017 6:36	55
4/4/2017 1:16	54	5/4/2017 2:21	53	6/4/2017 3:26	52	7/4/2017 4:31	52	8/4/2017 5:36	56	9/4/2017 6:41	55
4/4/2017 1:21	54	5/4/2017 2:26	51	6/4/2017 3:31	52	7/4/2017 4:36	52	8/4/2017 5:41	55	9/4/2017 6:46	55
4/4/2017 1:26	54	5/4/2017 2:31	57	6/4/2017 3:36	51	7/4/2017 4:41	52	8/4/2017 5:46	55	9/4/2017 6:51	56
4/4/2017 1:31	54	5/4/2017 2:36	52	6/4/2017 3:41	50	7/4/2017 4:46	54	8/4/2017 5:51	55	9/4/2017 6:56	55
4/4/2017 1:36	53	5/4/2017 2:41	53	6/4/2017 3:46	51	7/4/2017 4:51	54	8/4/2017 5:56	54	9/4/2017 7:01	57
4/4/2017 1:41	55	5/4/2017 2:46	52	6/4/2017 3:51	51	7/4/2017 4:56	54	8/4/2017 6:01	55	9/4/2017 7:06	56
4/4/2017 1:46	54	5/4/2017 2:51	52	6/4/2017 3:56	52	7/4/2017 5:01	52	8/4/2017 6:06	55	9/4/2017 7:11	56
4/4/2017 1:51	53	5/4/2017 2:56	52	6/4/2017 4:01	51	7/4/2017 5:06	51	8/4/2017 6:11	55	9/4/2017 7:16	57
4/4/2017 1:56	53	5/4/2017 3:01	52	6/4/2017 4:06	51	7/4/2017 5:11	53	8/4/2017 6:16	55	9/4/2017 7:21	56
4/4/2017 2:01	53	5/4/2017 3:06	52	6/4/2017 4:11	51	7/4/2017 5:16	53	8/4/2017 6:21	57	9/4/2017 7:26	57
4/4/2017 2:06	53	5/4/2017 3:11	58	6/4/2017 4:16	51	7/4/2017 5:21	53	8/4/2017 6:26	55	9/4/2017 7:31	57
4/4/2017 2:11	53	5/4/2017 3:16	52	6/4/2017 4:21	52	7/4/2017 5:26	52	8/4/2017 6:31	56	9/4/2017 7:36	57
4/4/2017 2:16	53	5/4/2017 3:21	52	6/4/2017 4:26	53	7/4/2017 5:31	53	8/4/2017 6:36	56	9/4/2017 7:41	57
4/4/2017 2:21	53	5/4/2017 3:26	54	6/4/2017 4:31	52	7/4/2017 5:36	53	8/4/2017 6:41	56	9/4/2017 7:46	57
4/4/2017 2:26	53	5/4/2017 3:31	51	6/4/2017 4:36	51	7/4/2017 5:41	53	8/4/2017 6:46	58	9/4/2017 7:51	57
4/4/2017 2:31	55	5/4/2017 3:36	52	6/4/2017 4:41	52	7/4/2017 5:46	53	8/4/2017 6:51	52	9/4/2017 7:56	57
4/4/2017 2:36	52	5/4/2017 3:41	52	6/4/2017 4:46	52	7/4/2017 5:51	53	8/4/2017 6:56	58	10/4/2017 0:01	56
4/4/2017 2:41	53	5/4/2017 3:46	54	6/4/2017 4:51	52	7/4/2017 5:56	53	8			

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
10/4/2017 2:41	55	11/4/2017 3:46	53	12/4/2017 4:51	55	13/4/2017 5:56	55	14/4/2017 23:01	47	16/4/2017 0:06	54
10/4/2017 2:46	55	11/4/2017 3:51	52	12/4/2017 4:56	55	13/4/2017 6:01	56	14/4/2017 23:06	57	16/4/2017 0:11	54
10/4/2017 2:51	55	11/4/2017 3:56	53	12/4/2017 5:01	55	13/4/2017 6:06	57	14/4/2017 23:11	58	16/4/2017 0:16	54
10/4/2017 2:56	55	11/4/2017 4:01	54	12/4/2017 5:06	55	13/4/2017 6:11	57	14/4/2017 23:16	57	16/4/2017 0:21	55
10/4/2017 3:01	55	11/4/2017 4:06	54	12/4/2017 5:11	56	13/4/2017 6:16	56	14/4/2017 23:21	57	16/4/2017 0:26	54
10/4/2017 3:06	55	11/4/2017 4:11	53	12/4/2017 5:16	56	13/4/2017 6:21	56	14/4/2017 23:26	57	16/4/2017 0:31	54
10/4/2017 3:11	55	11/4/2017 4:16	53	12/4/2017 5:21	56	13/4/2017 6:26	56	14/4/2017 23:31	45	16/4/2017 0:36	55
10/4/2017 3:16	56	11/4/2017 4:21	53	12/4/2017 5:26	56	13/4/2017 6:31	57	14/4/2017 23:36	58	16/4/2017 0:41	55
10/4/2017 3:21	55	11/4/2017 4:26	53	12/4/2017 5:31	56	13/4/2017 6:36	51	14/4/2017 23:41	58	16/4/2017 0:46	55
10/4/2017 3:26	54	11/4/2017 4:31	53	12/4/2017 5:36	55	13/4/2017 6:41	54	14/4/2017 23:46	57	16/4/2017 0:51	55
10/4/2017 3:31	56	11/4/2017 4:36	53	12/4/2017 5:41	56	13/4/2017 6:46	54	14/4/2017 23:51	58	16/4/2017 0:56	54
10/4/2017 3:36	57	11/4/2017 4:41	53	12/4/2017 5:46	55	13/4/2017 6:51	49	14/4/2017 23:56	57	16/4/2017 1:01	54
10/4/2017 3:41	56	11/4/2017 4:46	54	12/4/2017 5:51	55	13/4/2017 6:56	50	15/4/2017 0:01	57	16/4/2017 1:06	56
10/4/2017 3:46	55	11/4/2017 4:51	54	12/4/2017 5:56	56	13/4/2017 23:01	54	15/4/2017 0:06	57	16/4/2017 1:11	55
10/4/2017 3:51	55	11/4/2017 4:56	54	12/4/2017 6:01	56	13/4/2017 23:06	57	15/4/2017 0:11	57	16/4/2017 1:16	55
10/4/2017 3:56	55	11/4/2017 5:01	55	12/4/2017 6:06	56	13/4/2017 23:11	54	15/4/2017 0:16	57	16/4/2017 1:21	54
10/4/2017 4:01	57	11/4/2017 5:06	54	12/4/2017 6:11	56	13/4/2017 23:16	57	15/4/2017 0:21	56	16/4/2017 1:26	54
10/4/2017 4:06	54	11/4/2017 5:11	54	12/4/2017 6:16	56	13/4/2017 23:21	55	15/4/2017 0:26	57	16/4/2017 1:31	53
10/4/2017 4:11	55	11/4/2017 5:16	55	12/4/2017 6:21	56	13/4/2017 23:26	54	15/4/2017 0:31	56	16/4/2017 1:36	54
10/4/2017 4:16	54	11/4/2017 5:21	54	12/4/2017 6:26	57	13/4/2017 23:31	53	15/4/2017 0:36	56	16/4/2017 1:41	55
10/4/2017 4:21	56	11/4/2017 5:26	55	12/4/2017 6:31	58	13/4/2017 23:36	55	15/4/2017 0:41	57	16/4/2017 1:46	53
10/4/2017 4:26	55	11/4/2017 5:31	55	12/4/2017 6:36	53	13/4/2017 23:41	48	15/4/2017 0:46	57	16/4/2017 1:51	53
10/4/2017 4:31	55	11/4/2017 5:36	54	12/4/2017 6:41	52	13/4/2017 23:46	48	15/4/2017 0:51	56	16/4/2017 1:56	55
10/4/2017 4:36	55	11/4/2017 5:41	54	12/4/2017 6:46	58	13/4/2017 23:51	57	15/4/2017 0:56	57	16/4/2017 2:01	54
10/4/2017 4:41	54	11/4/2017 5:46	53	12/4/2017 6:51	58	13/4/2017 23:56	58	15/4/2017 1:01	57	16/4/2017 2:06	54
10/4/2017 4:46	56	11/4/2017 5:51	54	12/4/2017 6:56	58	14/4/2017 0:01	56	15/4/2017 1:06	56	16/4/2017 2:11	54
10/4/2017 4:51	55	11/4/2017 5:56	55	12/4/2017 23:01	39	14/4/2017 0:06	57	15/4/2017 1:11	57	16/4/2017 2:16	54
10/4/2017 4:56	56	11/4/2017 6:01	55	12/4/2017 23:06	57	14/4/2017 0:11	57	15/4/2017 1:16	57	16/4/2017 2:21	53
10/4/2017 5:01	55	11/4/2017 6:06	56	12/4/2017 23:11	43	14/4/2017 0:16	35	15/4/2017 1:21	57	16/4/2017 2:26	53
10/4/2017 5:06	56	11/4/2017 6:11	56	12/4/2017 23:16	57	14/4/2017 0:21	54	15/4/2017 1:26	56	16/4/2017 2:31	53
10/4/2017 5:11	56	11/4/2017 6:16	55	12/4/2017 23:21	57	14/4/2017 0:26	58	15/4/2017 1:31	57	16/4/2017 2:36	53
10/4/2017 5:16	56	11/4/2017 6:21	56	12/4/2017 23:26	58	14/4/2017 0:31	57	15/4/2017 1:36	57	16/4/2017 2:41	54
10/4/2017 5:21	55	11/4/2017 6:26	56	12/4/2017 23:31	57	14/4/2017 0:36	57	15/4/2017 1:41	57	16/4/2017 2:46	53
10/4/2017 5:26	55	11/4/2017 6:31	55	12/4/2017 23:36	57	14/4/2017 0:41	56	15/4/2017 1:46	57	16/4/2017 2:51	53
10/4/2017 5:31	55	11/4/2017 6:36	56	12/4/2017 23:41	57	14/4/2017 0:46	56	15/4/2017 1:51	57	16/4/2017 2:56	52
10/4/2017 5:36	55	11/4/2017 6:41	56	12/4/2017 23:46	57	14/4/2017 0:51	56	15/4/2017 1:56	58	16/4/2017 3:01	53
10/4/2017 5:41	55	11/4/2017 6:46	56	12/4/2017 23:51	57	14/4/2017 0:56	52	15/4/2017 2:01	56	16/4/2017 3:06	53
10/4/2017 5:46	57	11/4/2017 6:51	56	12/4/2017 23:56	57	14/4/2017 1:01	58	15/4/2017 2:06	55	16/4/2017 3:11	53
10/4/2017 5:51	57	11/4/2017 6:56	56	13/4/2017 0:01	57	14/4/2017 1:06	56	15/4/2017 2:11	55	16/4/2017 3:16	53
10/4/2017 5:56	57	11/4/2017 23:01	45	13/4/2017 0:06	57	14/4/2017 1:11	56	15/4/2017 2:16	56	16/4/2017 3:21	52
10/4/2017 6:01	57	11/4/2017 23:06	58	13/4/2017 0:11	57	14/4/2017 1:16	57	15/4/2017 2:21	56	16/4/2017 3:26	53
10/4/2017 6:06	56	11/4/2017 23:11	57	13/4/2017 0:16	57	14/4/2017 1:21	51	15/4/2017 2:26	56	16/4/2017 3:31	53
10/4/2017 6:11	56	11/4/2017 23:16	58	13/4/2017 0:21	57	14/4/2017 1:26	57	15/4/2017 2:31	56	16/4/2017 3:36	53
10/4/2017 6:16	56	11/4/2017 23:21	57	13/4/2017 0:26	57	14/4/2017 1:31	57	15/4/2017 2:36	56	16/4/2017 3:41	53
10/4/2017 6:21	57	11/4/2017 23:26	57	13/4/2017 0:31	57	14/4/2017 1:36	56	15/4/2017 2:41	56	16/4/2017 3:46	52
10/4/2017 6:26	57	11/4/2017 23:31	57	13/4/2017 0:36	57	14/4/2017 1:41	56	15/4/2017 2:46	56	16/4/2017 3:51	53
10/4/2017 6:31	57	11/4/2017 23:36	57	13/4/2017 0:41	56	14/4/2017 1:46	56	15/4/2017 2:51	56	16/4/2017 3:56	54
10/4/2017 6:36	47	11/4/2017 23:41	57	13/4/2017 0:46	58	14/4/2017 1:51	57	15/4/2017 2:56	56	16/4/2017 4:01	53
10/4/2017 6:41	57	11/4/2017 23:46	57	13/4/2017 0:51	57	14/4/2017 1:56	51	15/4/2017 3:01	56	16/4/2017 4:06	53
10/4/2017 6:46	57	11/4/2017 23:51	58	13/4/2017 0:56	57	14/4/2017 2:01	49	15/4/2017 3:06	55	16/4/2017 4:11	52
10/4/2017 6:51	57	11/4/2017 23:56	57	13/4/2017 1:01	58	14/4/2017 2:06	56	15/4/2017 3:11	56	16/4/2017 4:16	53
10/4/2017 6:56	45	12/4/2017 0:01	57	13/4/2017 1:06	58	14/4/2017 2:11	57	15/4/2017 3:16	56	16/4/2017 4:21	53
10/4/2017 23:01	56	12/4/2017 0:06	58	13/4/2017 1:11	57	14/4/2017 2:16	56	15/4/2017 3:21	56	16/4/2017 4:26	53
10/4/2017 23:06	57	12/4/2017 0:11	57	13/4/2017 1:16	56	14/4/2017 2:21	56	15/4/2017 3:26	56	16/4/2017 4:31	52
10/4/2017 23:11	56	12/4/2017 0:16	57	13/4/2017 1:21	56	14/4/2017 2:26	56	15/4/2017 3:31	55	16/4/2017 4:36	52
10/4/2017 23:16	57	12/4/2017 0:21	56	13/4/2017 1:26	57	14/4/2017 2:31	56	15/4/2017 3:36	55	16/4/2017 4:41	51
10/4/2017 23:21	57	12/4/2017 0:26	56	13/4/2017 1:31	57	14/4/2017 2:36	56	15/4/2017 3:41	57	16/4/2017 4:46	52
10/4/2017 23:26	56	12/4/2017 0:31	58	13/4/2017 1:36	57	14/4/2017 2:41	56	15/4/2017 3:46	56	16/4/2017 4:51	52
10/4/2017 23:31	56	12/4/2017 0:36	56	13/4/2017 1:41	57	14/4/2017 2:46	56	15/4/2017 3:51	56	16/4/2017 4:56	52
10/4/2017 23:36	56	12/4/2017 0:41	56	13/4/2017 1:46	57	14/4/2017 2:51	56	15/4/2017 3:56	55	16/4/2017 5:01	54
10/4/2017 23:41	57	12/4/2017 0:46	57	13/4/2017 1:51	56	14/4/2017 2:56	56	15/4/2017 4:01	55	16/4/2017 5:06	53
10/4/2017 23:46	57	12/4/2017 0:51	56	13/4/2017 1:56	56	14/4/2017 3:01	57	15/4/2017 4:06	55	16/4/2017 5:11	53
10/4/2017 23:51	57	12/4/2017 0:56	56	13/4/2017 2:01	56	14/4/2017 3:06	56	15/4/2017 4:11	56	16/4/2017 5:16	53
10/4/2017 23:56	56	12/4/2017 1:01	56	13/4/2017 2:06	56	14/4/2017 3:11	56	15/4/2017 4:16	58	16/4/2017 5:21	53
11/4/2017 0:01	56	12/4/2017 1:06	57	13/4/2017 2:11	56	14/4/2017 3:16	56	15/4/2017 4:21	57	16/4/2017 5:26	52
11/4/2017 0:06	55	12/4/2017 1:11	58	13/4/2017 2:16	56	14/4/2017 3:21	56	15/4/2017 4:26	56	16/4/2017 5:31	52
11/4/2017 0:11	55	12/4/2017 1:16	56	13/4/2017 2:21	56	14/4/2017 3:26	56	15/4/2017 4:31	56	16/4/2017 5:36	52
11/4/2017 0:16	56	12/4/2017 1:21	57	13/4/2017 2:26	56	14/4/2017 3:31	56	15/4/2017 4:36	57	16/4/2017 5:41	53
11/4/2017 0:21	56	12/4/2017 1:26	57	13/4/2017 2:31	56	14/4/2017 3:36	56	15/4/2017 4:41	56	16/4/2017 5:46	53
11/4/2017 0:26	56	12/4/2017 1:31	57	13/4/2017 2:36	57	14/4/2017 3:41	56	15/4/2017 4:46	56	16/4/2017 5:51	53
11/4/2017 0:31	56	12/4/2017 1:36	57	13/4/2017 2:41	56	14/4/2017 3:46	57	15/4/2017 4:51	56	16/4/2017 5:56	56
11/4/2017 0:36	56	12/4/2017 1:41	55	13/4/2017 2:46	56	14/4/2017 3:51	57	15/4/2017 4:56	56	16/4/2017 6:01	53
11/4/2017 0:41	55	12/4/2017 1:46	56	13/4/2017 2:51	56	14/4/2017 3:56	58	15/4/2017 5:01	56	16/4/2017 6:06	55
11/4/2017 0:46	57	12/4/2017 1:51	56	13/4/2017 2:56	56	14/4/2017 4:01	57	15/4/2017 5:06	57	16/4/2017 6:11	56
11/4/2017 0:51	56	12/4/2017 1:56	55	13/4/2017 3:01	56	14/4/2017 4:06	57	15/4/2017 5:11	56	16/4/2017 6:16	54
11/4/2017 0:56	55	12/4/2017 2:01	55	13/4/2017 3:							

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)	
17/4/2017 1:11	54	18/4/2017 2:21	52
17/4/2017 1:16	54	18/4/2017 2:21	53
17/4/2017 1:21	54	18/4/2017 2:26	53
17/4/2017 1:26	54	18/4/2017 2:31	53
17/4/2017 1:31	53	18/4/2017 2:36	53
17/4/2017 1:36	53	18/4/2017 2:41	53
17/4/2017 1:41	54	18/4/2017 2:46	53
17/4/2017 1:46	53	18/4/2017 2:51	52
17/4/2017 1:51	53	18/4/2017 2:56	52
17/4/2017 1:56	53	18/4/2017 3:01	53
17/4/2017 2:01	53	18/4/2017 3:06	53
17/4/2017 2:06	53	18/4/2017 3:11	52
17/4/2017 2:11	54	18/4/2017 3:16	53
17/4/2017 2:16	53	18/4/2017 3:21	53
17/4/2017 2:21	54	18/4/2017 3:26	53
17/4/2017 2:26	54	18/4/2017 3:31	53
17/4/2017 2:31	53	18/4/2017 3:36	53
17/4/2017 2:36	53	18/4/2017 3:41	54
17/4/2017 2:41	55	18/4/2017 3:46	53
17/4/2017 2:46	53	18/4/2017 3:51	53
17/4/2017 2:51	53	18/4/2017 3:56	53
17/4/2017 2:56	52	18/4/2017 4:01	53
17/4/2017 3:01	53	18/4/2017 4:06	53
17/4/2017 3:06	53	18/4/2017 4:11	55
17/4/2017 3:11	53	18/4/2017 4:16	53
17/4/2017 3:16	53	18/4/2017 4:21	53
17/4/2017 3:21	53	18/4/2017 4:26	53
17/4/2017 3:26	54	18/4/2017 4:31	54
17/4/2017 3:31	55	18/4/2017 4:36	53
17/4/2017 3:36	53	18/4/2017 4:41	53
17/4/2017 3:41	52	18/4/2017 4:46	53
17/4/2017 3:46	52	18/4/2017 4:51	53
17/4/2017 3:51	52	18/4/2017 4:56	54
17/4/2017 3:56	53	18/4/2017 5:01	54
17/4/2017 4:01	52	18/4/2017 5:06	54
17/4/2017 4:06	54	18/4/2017 5:11	54
17/4/2017 4:11	52	18/4/2017 5:16	53
17/4/2017 4:16	53	18/4/2017 5:21	53
17/4/2017 4:21	53	18/4/2017 5:26	53
17/4/2017 4:26	52	18/4/2017 5:31	54
17/4/2017 4:31	52	18/4/2017 5:36	53
17/4/2017 4:36	53	18/4/2017 5:41	54
17/4/2017 4:41	53	18/4/2017 5:46	55
17/4/2017 4:46	53	18/4/2017 5:51	54
17/4/2017 4:51	53	18/4/2017 5:56	54
17/4/2017 4:56	54	18/4/2017 6:01	54
17/4/2017 5:01	54	18/4/2017 6:06	55
17/4/2017 5:06	53	18/4/2017 6:11	56
17/4/2017 5:11	53	18/4/2017 6:16	55
17/4/2017 5:16	54	18/4/2017 6:21	55
17/4/2017 5:21	54	18/4/2017 6:26	55
17/4/2017 5:26	53	18/4/2017 6:31	56
17/4/2017 5:31	53	18/4/2017 6:36	55
17/4/2017 5:36	53	18/4/2017 6:41	56
17/4/2017 5:41	52	18/4/2017 6:46	56
17/4/2017 5:46	54	18/4/2017 6:51	57
17/4/2017 5:51	54	18/4/2017 6:56	57
17/4/2017 5:56	53	18/4/2017 7:01	58
17/4/2017 6:01	53	18/4/2017 7:06	57
17/4/2017 6:06	54	18/4/2017 7:11	47
17/4/2017 6:11	54	18/4/2017 7:16	56
17/4/2017 6:16	54	18/4/2017 7:21	56
17/4/2017 6:21	54	18/4/2017 7:26	55
17/4/2017 6:26	56	18/4/2017 7:31	56
17/4/2017 6:31	54	18/4/2017 7:36	56
17/4/2017 6:36	57	18/4/2017 7:41	56
17/4/2017 6:41	45	18/4/2017 7:46	55
17/4/2017 6:46	55	18/4/2017 7:51	56
17/4/2017 6:51	55	18/4/2017 7:56	56
17/4/2017 6:56	55	19/4/2017 0:01	56
17/4/2017 23:01	56	19/4/2017 0:06	55
17/4/2017 23:06	55	19/4/2017 0:11	55
17/4/2017 23:11	56	19/4/2017 0:16	57
17/4/2017 23:16	55	19/4/2017 0:21	56
17/4/2017 23:21	55	19/4/2017 0:26	55
17/4/2017 23:26	55	19/4/2017 0:31	56
17/4/2017 23:31	55	19/4/2017 0:36	55
17/4/2017 23:36	55	19/4/2017 0:41	55
17/4/2017 23:41	55	19/4/2017 0:46	55
17/4/2017 23:46	55	19/4/2017 0:51	54
17/4/2017 23:51	55	19/4/2017 0:56	55
17/4/2017 23:56	54	19/4/2017 1:01	55
18/4/2017 0:01	55	19/4/2017 1:06	56
18/4/2017 0:06	57	19/4/2017 1:11	55
18/4/2017 0:11	55	19/4/2017 1:16	55
18/4/2017 0:16	55	19/4/2017 1:21	54
18/4/2017 0:21	55	19/4/2017 1:26	54
18/4/2017 0:26	54	19/4/2017 1:31	54
18/4/2017 0:31	54	19/4/2017 1:36	54
18/4/2017 0:36	55	19/4/2017 1:41	54
18/4/2017 0:41	54	19/4/2017 1:46	54
18/4/2017 0:46	54	19/4/2017 1:51	54
18/4/2017 0:51	54	19/4/2017 1:56	54
18/4/2017 0:56	55	19/4/2017 2:01	53
18/4/2017 1:01	55	19/4/2017 2:06	54
18/4/2017 1:06	54	19/4/2017 2:11	54
18/4/2017 1:11	53	19/4/2017 2:16	53
18/4/2017 1:16	54	19/4/2017 2:21	54
18/4/2017 1:21	54	19/4/2017 2:26	54
18/4/2017 1:26	54	19/4/2017 2:31	53
18/4/2017 1:31	54	19/4/2017 2:36	54
18/4/2017 1:36	54	19/4/2017 2:41	53
18/4/2017 1:41	54	19/4/2017 2:46	53
18/4/2017 1:46	54	19/4/2017 2:51	53
18/4/2017 1:51	54	19/4/2017 2:56	53
18/4/2017 1:56	54	20/4/2017 3:01	53
18/4/2017 2:01	53	20/4/2017 3:06	53
18/4/2017 2:06	54	20/4/2017 3:11	54
18/4/2017 2:11	54	20/4/2017 3:16	54
18/4/2017 2:16	53	20/4/2017 3:21	54
18/4/2017 2:21	54	20/4/2017 3:26	54
18/4/2017 2:26	54	20/4/2017 3:31	54
18/4/2017 2:31	53	20/4/2017 3:36	54
18/4/2017 2:36	53	20/4/2017 3:41	54
18/4/2017 2:41	53	20/4/2017 3:46	54
18/4/2017 2:46	54	20/4/2017 3:51	54
18/4/2017 2:51	54	20/4/2017 3:56	54
18/4/2017 2:56	53	20/4/2017 4:01	55
18/4/2017 3:01	53	20/4/2017 4:06	55
18/4/2017 3:06	53	20/4/2017 4:11	54
18/4/2017 3:11	53	20/4/2017 4:16	54
18/4/2017 3:16	52	20/4/2017 4:21	55
20/4/2017 4:26	54		
20/4/2017 4:31	55		
20/4/2017 4:36	55		
20/4/2017 4:41	54		
20/4/2017 4:46	53		
20/4/2017 4:51	53		
20/4/2017 4:56	53		
20/4/2017 5:01	53		
20/4/2017 5:06	53		
20/4/2017 5:11	53		
20/4/2017 5:16	53		
20/4/2017 5:21	53		
20/4/2017 5:26	54		
20/4/2017 5:31	54		
20/4/2017 5:36	54		
20/4/2017 5:41	55		
20/4/2017 5:46	54		
20/4/2017 5:51	55		
20/4/2017 5:56	55		
20/4/2017 6:01	55		
20/4/2017 6:06	56		
20/4/2017 6:11	56		
20/4/2017 6:16	57		
20/4/2017 6:21	56		
20/4/2017 6:26	56		
20/4/2017 6:31	57		
20/4/2017 6:36	57		
20/4/2017 6:41	56		
20/4/2017 6:46	56		
20/4/2017 6:51	56		
20/4/2017 6:56	56		
20/4/2017 7:01	57		
20/4/2017 7:06	58		
20/4/2017 7:11	57		
20/4/2017 7:16	57		
20/4/2017 7:21	57		
20/4/2017 7:26	56		
20/4/2017 7:31	56		
20/4/2017 7:36	56		
20/4/2017 7:41	56		
20/4/2017 7:46	56		
20/4/2017 7:51	56		
20/4/2017 7:56	56		
20/4/2017 8:01	56		
20/4/2017 8:06	56		
20/4/2017 8:11	56		
20/4/2017 8:16	56		
20/4/2017 8:21	56		
20/4/2017 8:26	56		
20/4/2017 8:31	56		
20/4/2017 8:36	56		
20/4/2017 8:41	56		
20/4/2017 8:46	56		
20/4/2017 8:51	56		
20/4/2017 8:56	56		
20/4/2017 9:01	56		
20/4/2017 9:06	56		
20/4/2017 9:11	56		
20/4/2017 9:16	56		
20/4/2017 9:21	56		
20/4/2017 9:26	56		
20/4/2017 9:31	56		
20/4/2017 9:36	56		
20/4/2017 9:41	56		
20/4/2017 9:46	56		
20/4/2017 9:51	56		
20/4/2017 9:56	56		
20/4/2017 10:01	56		
20/4/2017 10:06	56		
20/4/2017 10:11	56		
20/4/2017 10:16	56		
20/4/2017 10:21	56		
20/4/2017 10:26	56		
20/4/2017 10:31	56		
20/4/2017 10:36	56		
20/4/2017 10:41	56		
20/4/2017 10:46	56		
20/4/2017 10:51	56		
20/4/2017 10:56	56		
20/4/2017 11:01	56		
20/4/2017 11:06	56		
20/4/2017 11:11	56		
20/4/2017 11:16	56		
20/4/2017 11:21	56		
20/4/2017 11:26	56		
20/4/2017 11:31	56		
20/4/2017 11:36	56		
20/4/2017 11:41	56		
20/4/2017 11:46	56		
20/4/2017 11:51	56		
20/4/2017 11:56	56		
20/4/2017 12:01	56		
20/4/2017 12:06	56		
20/4/2017 12:11	56		
20/4/2017 12:16	56		
20/4/2017 12:21	56		
20/4/2017 12:26	56		
20/4/2017 12:31	56		
20/4/2017 12:36	56		
20/4/2017 12:41	56		
20/4/2017 12:46	56		
20/4/2017 12:51	56		
20/4/2017 12:56	56		
20/4/2017 13:01	56		
20/4/2017 13:06	56		
20/4/2017 13:11	56		
20/4/2017 13:16	56		
20/4/2017 13:21	56		
20/4/2017 13:26	56		
20/4/2017 13:31	56		
20/4/2017 13:36	56		
20/4/2017 13:41	56		
20/4/2017 13:46	56		
20/4/2017 13:51	56		
20/4/2017 13:56	56		
20/4/2017 14:01	56		
20/4/2017 14:06	56		
20/4/2017 14:11	56		
20/4/2017 14:16	56		
20/4/2017 14:21	56		
20/4/2017 14:26	56		
20/4/2017 14:31	56		
20/4/2017 14:36	56		
20/4/2017 14:41	56		
20/4/2017 14:46	56		
20/4/2017 14:51	56		
20/4/2017 14:56	56		
20/4/2017 15:01	56		
20/4/2017 15:06	56		
20/4/2017 15:11	56		
20/4/2017 15:16	56		
20/4/2017 15:21	56		
20/4/2017 15:26	56		
20/4/2017 15:31	56		
20/4/2017 15:36	56		
20/4/2017 15:41	56		
20/4/2017 15:46	56		
20/4/2017 15:51	56		
20/4/2017 15:56	56		
20/4/2017 16:01	56		
20/4/2017 16:06	56		
20/4/2017 16:11			

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)	
23/4/2017 23:41	55	25/4/2017 0:46	54
23/4/2017 23:46	55	25/4/2017 0:51	54
23/4/2017 23:51	55	25/4/2017 0:56	54
23/4/2017 23:56	54	25/4/2017 1:01	54
24/4/2017 0:01	54	25/4/2017 1:06	53
24/4/2017 0:06	54	25/4/2017 1:11	53
24/4/2017 0:11	55	25/4/2017 1:16	53
24/4/2017 0:16	54	25/4/2017 1:21	53
24/4/2017 0:21	54	25/4/2017 1:26	53
24/4/2017 0:26	53	25/4/2017 1:31	53
24/4/2017 0:31	54	25/4/2017 1:36	53
24/4/2017 0:36	53	25/4/2017 1:41	53
24/4/2017 0:41	53	25/4/2017 1:46	53
24/4/2017 0:46	55	25/4/2017 1:51	52
24/4/2017 0:51	53	25/4/2017 1:56	52
24/4/2017 0:56	52	25/4/2017 2:01	53
24/4/2017 1:01	53	25/4/2017 2:06	53
24/4/2017 1:06	53	25/4/2017 2:11	52
24/4/2017 1:11	53	25/4/2017 2:16	52
24/4/2017 1:16	53	25/4/2017 2:21	53
24/4/2017 1:21	53	25/4/2017 2:26	52
24/4/2017 1:26	52	25/4/2017 2:31	52
24/4/2017 1:31	52	25/4/2017 2:36	51
24/4/2017 1:36	52	25/4/2017 2:41	52
24/4/2017 1:41	52	25/4/2017 2:46	52
24/4/2017 1:46	52	25/4/2017 2:51	52
24/4/2017 1:51	52	25/4/2017 2:56	52
24/4/2017 1:56	52	25/4/2017 3:01	52
24/4/2017 2:01	52	25/4/2017 3:06	51
24/4/2017 2:06	52	25/4/2017 3:11	52
24/4/2017 2:11	52	25/4/2017 3:16	52
24/4/2017 2:16	52	25/4/2017 3:21	51
24/4/2017 2:21	52	25/4/2017 3:26	51
24/4/2017 2:26	52	25/4/2017 3:31	53
24/4/2017 2:31	51	25/4/2017 3:36	52
24/4/2017 2:36	52	25/4/2017 3:41	52
24/4/2017 2:41	51	25/4/2017 3:46	52
24/4/2017 2:46	51	25/4/2017 3:51	52
24/4/2017 2:51	52	25/4/2017 3:56	51
24/4/2017 2:56	52	25/4/2017 4:01	51
24/4/2017 3:01	51	25/4/2017 4:06	52
24/4/2017 3:06	51	25/4/2017 4:11	51
24/4/2017 3:11	50	25/4/2017 4:16	51
24/4/2017 3:16	51	25/4/2017 4:21	53
24/4/2017 3:21	50	25/4/2017 4:26	52
24/4/2017 3:26	51	25/4/2017 4:31	52
24/4/2017 3:31	50	25/4/2017 4:36	51
24/4/2017 3:36	51	25/4/2017 4:41	51
24/4/2017 3:41	51	25/4/2017 4:46	52
24/4/2017 3:46	52	25/4/2017 4:51	52
24/4/2017 3:51	51	25/4/2017 4:56	52
24/4/2017 3:56	51	25/4/2017 5:01	52
24/4/2017 4:01	50	25/4/2017 5:06	52
24/4/2017 4:06	50	25/4/2017 5:11	52
24/4/2017 4:11	51	25/4/2017 5:16	52
24/4/2017 4:16	53	25/4/2017 5:21	51
24/4/2017 4:21	51	25/4/2017 5:26	52
24/4/2017 4:26	51	25/4/2017 5:31	52
24/4/2017 4:31	51	25/4/2017 5:36	53
24/4/2017 4:36	50	25/4/2017 5:41	55
24/4/2017 4:41	51	25/4/2017 5:46	53
24/4/2017 4:46	51	25/4/2017 5:51	60
24/4/2017 4:51	52	25/4/2017 5:56	53
24/4/2017 4:56	52	25/4/2017 6:01	53
24/4/2017 5:01	52	25/4/2017 6:06	57
24/4/2017 5:06	52	25/4/2017 6:11	53
24/4/2017 5:11	55	25/4/2017 6:16	55
24/4/2017 5:16	52	25/4/2017 6:21	54
24/4/2017 5:21	52	25/4/2017 6:26	54
24/4/2017 5:26	53	25/4/2017 6:31	54
24/4/2017 5:31	52	25/4/2017 6:36	55
24/4/2017 5:36	53	25/4/2017 6:41	55
24/4/2017 5:41	54	25/4/2017 6:46	56
24/4/2017 5:46	54	25/4/2017 6:51	58
24/4/2017 5:51	53	25/4/2017 6:56	57
24/4/2017 5:56	52	25/4/2017 23:01	56
24/4/2017 6:01	54	25/4/2017 23:06	56
24/4/2017 6:06	55	25/4/2017 23:11	56
24/4/2017 6:11	55	25/4/2017 23:16	55
24/4/2017 6:16	55	25/4/2017 23:21	55
24/4/2017 6:21	55	25/4/2017 23:26	55
24/4/2017 6:26	55	25/4/2017 23:31	55
24/4/2017 6:31	55	25/4/2017 23:36	54
24/4/2017 6:36	55	25/4/2017 23:41	55
24/4/2017 6:41	55	25/4/2017 23:46	55
24/4/2017 6:46	55	25/4/2017 23:51	56
24/4/2017 6:51	55	25/4/2017 23:56	55
24/4/2017 6:56	56	26/4/2017 0:01	55
24/4/2017 23:01	57	26/4/2017 0:06	56
24/4/2017 23:06	56	26/4/2017 0:11	54
24/4/2017 23:11	56	26/4/2017 0:16	55
24/4/2017 23:16	55	26/4/2017 0:21	55
24/4/2017 23:21	55	26/4/2017 0:26	55
24/4/2017 23:26	55	26/4/2017 0:31	54
24/4/2017 23:31	55	26/4/2017 0:36	54
24/4/2017 23:36	56	26/4/2017 0:41	55
24/4/2017 23:41	55	26/4/2017 0:46	54
24/4/2017 23:46	55	26/4/2017 0:51	54
24/4/2017 23:51	55	26/4/2017 0:56	57
24/4/2017 23:56	54	26/4/2017 1:01	54
25/4/2017 0:01	55	26/4/2017 1:06	56
25/4/2017 0:06	55	26/4/2017 1:11	54
25/4/2017 0:11	55	26/4/2017 1:16	53
25/4/2017 0:16	55	26/4/2017 1:21	54
25/4/2017 0:21	55	26/4/2017 1:26	54
25/4/2017 0:26	56	26/4/2017 1:31	54
25/4/2017 0:31	55	26/4/2017 1:36	53
25/4/2017 0:36	55	26/4/2017 1:41	54
25/4/2017 0:41	53	26/4/2017 1:46	54
		26/4/2017 1:51	53
		26/4/2017 1:56	52
		26/4/2017 2:01	57
		26/4/2017 2:06	53
		26/4/2017 2:11	52
		26/4/2017 2:16	52
		26/4/2017 2:21	53
		26/4/2017 2:26	52
		26/4/2017 2:31	52
		26/4/2017 2:36	52
		26/4/2017 2:41	52
		26/4/2017 2:46	52
		26/4/2017 2:51	53
		26/4/2017 2:56	53
		26/4/2017 3:01	53
		26/4/2017 3:06	52
		26/4/2017 3:11	53
		26/4/2017 3:16	53
		26/4/2017 3:21	52
		26/4/2017 3:26	52
		26/4/2017 3:31	52
		26/4/2017 3:36	51
		26/4/2017 3:41	52
		26/4/2017 3:46	52
		26/4/2017 3:51	52
		26/4/2017 3:56	53
		26/4/2017 4:01	52
		26/4/2017 4:06	51
		26/4/2017 4:11	52
		26/4/2017 4:16	52
		26/4/2017 4:21	52
		26/4/2017 4:26	53
		26/4/2017 4:31	52
		26/4/2017 4:36	52
		26/4/2017 4:41	52
		26/4/2017 4:46	52
		26/4/2017 4:51	52
		26/4/2017 4:56	52
		26/4/2017 5:01	53
		26/4/2017 5:06	53
		26/4/2017 5:11	53
		26/4/2017 5:16	53
		26/4/2017 5:21	53
		26/4/2017 5:26	56
		26/4/2017 5:31	47
		26/4/2017 5:36	55
		26/4/2017 5:41	53
		26/4/2017 5:46	53
		26/4/2017 5:51	54
		26/4/2017 5:56	53
		26/4/2017 6:01	38
		26/4/2017 6:06	57
		26/4/2017 6:11	54
		26/4/2017 6:16	54
		26/4/2017 6:21	55
		26/4/2017 6:26	54
		26/4/2017 6:31	55
		26/4/2017 6:36	55
		26/4/2017 6:41	55
		26/4/2017 6:46	56
		26/4/2017 6:51	56
		26/4/2017 6:56	56
		26/4/2017 23:01	56
		26/4/2017 23:06	58
		26/4/2017 23:11	53
		26/4/2017 23:16	58
		26/4/2017 23:21	57
		26/4/2017 23:26	56
		26/4/2017 23:31	56
		26/4/2017 23:36	57
		26/4/2017 23:41	56
		26/4/2017 23:46	56
		26/4/2017 23:51	56
		26/4/2017 23:56	56

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)							
Normal Day 07:00-19:00									
27/3/2017 7:01	66	31/3/2017 13:01	67	7/4/2017 7:31	67	12/4/2017 14:01	68	21/4/2017 8:31	66
27/3/2017 7:31	65	31/3/2017 13:31	69	7/4/2017 8:01	66	12/4/2017 14:31	69	21/4/2017 9:01	66
27/3/2017 8:01	64	31/3/2017 14:01	66	7/4/2017 8:31	66	12/4/2017 15:01	68	21/4/2017 9:31	66
27/3/2017 8:31	64	31/3/2017 14:31	67	7/4/2017 9:01	66	12/4/2017 15:31	66	21/4/2017 10:01	67
27/3/2017 9:01	66	31/3/2017 15:01	65	7/4/2017 9:31	66	12/4/2017 16:01	68	21/4/2017 10:31	68
27/3/2017 9:31	67	31/3/2017 15:31	65	7/4/2017 10:01	65	12/4/2017 16:31	55	21/4/2017 11:01	67
27/3/2017 10:01	68	31/3/2017 16:01	66	7/4/2017 10:31	66	12/4/2017 17:01	69	21/4/2017 11:31	67
27/3/2017 10:31	67	31/3/2017 16:31	67	7/4/2017 11:01	66	12/4/2017 17:31	67	21/4/2017 12:01	66
27/3/2017 11:01	67	31/3/2017 17:01	66	7/4/2017 11:31	67	12/4/2017 18:01	67	21/4/2017 12:31	67
27/3/2017 11:31	67	31/3/2017 17:31	68	7/4/2017 12:01	64	12/4/2017 18:31	66	21/4/2017 13:01	68
27/3/2017 12:01	67	31/3/2017 18:01	67	7/4/2017 12:31	63	13/4/2017 7:01	67	21/4/2017 13:31	67
27/3/2017 12:31	67	31/3/2017 18:31	66	7/4/2017 13:01	66	13/4/2017 7:31	67	21/4/2017 14:01	67
27/3/2017 13:01	67	1/4/2017 7:01	66	7/4/2017 13:31	67	13/4/2017 8:01	68	21/4/2017 14:31	66
27/3/2017 13:31	68	1/4/2017 7:31	67	7/4/2017 14:01	66	13/4/2017 8:31	65	21/4/2017 15:01	67
27/3/2017 14:01	68	1/4/2017 8:01	67	7/4/2017 14:31	65	13/4/2017 9:01	67	21/4/2017 15:31	65
27/3/2017 14:31	68	1/4/2017 8:31	68	7/4/2017 15:01	65	13/4/2017 9:31	66	21/4/2017 16:01	69
27/3/2017 15:01	68	1/4/2017 9:01	68	7/4/2017 15:31	65	13/4/2017 10:01	66	21/4/2017 16:31	68
27/3/2017 15:31	68	1/4/2017 9:31	68	7/4/2017 16:01	66	13/4/2017 10:31	67	21/4/2017 17:01	67
27/3/2017 16:01	67	1/4/2017 10:01	67	7/4/2017 16:31	67	13/4/2017 11:01	66	21/4/2017 17:31	67
27/3/2017 16:31	67	1/4/2017 10:31	66	7/4/2017 17:01	67	13/4/2017 11:31	68	21/4/2017 18:01	66
27/3/2017 17:01	67	1/4/2017 11:01	67	7/4/2017 17:31	66	13/4/2017 12:01	67	21/4/2017 18:31	64
27/3/2017 17:31	66	1/4/2017 11:31	65	7/4/2017 18:01	66	13/4/2017 12:31	67	22/4/2017 7:01	66
27/3/2017 18:01	66	1/4/2017 12:01	65	7/4/2017 18:31	66	13/4/2017 13:01	67	22/4/2017 7:31	66
27/3/2017 18:31	66	1/4/2017 12:31	66	8/4/2017 7:01	66	13/4/2017 13:31	68	22/4/2017 8:01	67
28/3/2017 7:01	66	1/4/2017 13:01	67	8/4/2017 7:31	69	13/4/2017 14:01	68	22/4/2017 8:31	67
28/3/2017 7:31	66	1/4/2017 13:31	68	8/4/2017 8:01	67	13/4/2017 14:31	68	22/4/2017 9:01	68
28/3/2017 8:01	66	1/4/2017 14:01	66	8/4/2017 8:31	68	13/4/2017 15:01	67	22/4/2017 9:31	67
28/3/2017 8:31	66	1/4/2017 14:31	66	8/4/2017 9:01	68	13/4/2017 15:31	67	22/4/2017 10:01	68
28/3/2017 9:01	66	1/4/2017 15:01	68	8/4/2017 9:31	67	13/4/2017 16:01	68	22/4/2017 10:31	68
28/3/2017 9:31	65	1/4/2017 15:31	66	8/4/2017 10:01	68	13/4/2017 16:31	67	22/4/2017 11:01	67
28/3/2017 10:01	65	1/4/2017 16:01	67	8/4/2017 10:31	66	13/4/2017 17:01	67	22/4/2017 11:31	66
28/3/2017 10:31	66	1/4/2017 16:31	67	8/4/2017 11:01	65	13/4/2017 17:31	67	22/4/2017 12:01	66
28/3/2017 11:01	66	1/4/2017 17:01	67	8/4/2017 11:31	64	13/4/2017 18:01	66	22/4/2017 12:31	68
28/3/2017 11:31	66	1/4/2017 17:31	66	8/4/2017 12:01	66	13/4/2017 18:31	64	22/4/2017 13:01	68
28/3/2017 12:01	66	1/4/2017 18:01	66	8/4/2017 12:31	68	18/4/2017 7:01	66	22/4/2017 13:31	66
28/3/2017 12:31	66	1/4/2017 18:31	66	8/4/2017 13:01	68	18/4/2017 7:31	67	22/4/2017 14:01	65
28/3/2017 13:01	67	3/4/2017 7:01	67	8/4/2017 13:31	68	18/4/2017 8:01	66	22/4/2017 14:31	67
28/3/2017 13:31	67	3/4/2017 7:31	67	8/4/2017 14:01	68	18/4/2017 8:31	66	22/4/2017 15:01	68
28/3/2017 14:01	66	3/4/2017 8:01	67	8/4/2017 14:31	67	18/4/2017 9:01	67	22/4/2017 15:31	68
28/3/2017 14:31	67	3/4/2017 8:31	67	8/4/2017 15:01	67	18/4/2017 9:31	67	22/4/2017 16:01	67
28/3/2017 15:01	67	3/4/2017 9:01	67	8/4/2017 15:31	67	18/4/2017 10:01	67	22/4/2017 16:31	67
28/3/2017 15:31	67	3/4/2017 9:31	68	8/4/2017 16:01	67	18/4/2017 10:31	67	22/4/2017 17:01	67
28/3/2017 16:01	67	3/4/2017 10:01	67	8/4/2017 16:31	67	18/4/2017 11:01	67	22/4/2017 17:31	67
28/3/2017 16:31	67	3/4/2017 10:31	67	8/4/2017 17:01	66	18/4/2017 11:31	66	22/4/2017 18:01	67
28/3/2017 17:01	67	3/4/2017 11:01	67	8/4/2017 17:31	67	18/4/2017 12:01	66	22/4/2017 18:31	66
28/3/2017 17:31	66	3/4/2017 11:31	66	8/4/2017 18:01	66	18/4/2017 12:31	66	24/4/2017 7:01	66
28/3/2017 18:01	66	3/4/2017 12:01	66	8/4/2017 18:31	66	18/4/2017 13:01	66	24/4/2017 7:31	64
28/3/2017 18:31	66	3/4/2017 12:31	67	10/4/2017 7:01	66	18/4/2017 13:31	68	24/4/2017 8:01	66
29/3/2017 7:01	66	3/4/2017 13:01	66	10/4/2017 7:31	66	18/4/2017 14:01	67	24/4/2017 8:31	66
29/3/2017 7:31	66	3/4/2017 13:31	67	10/4/2017 8:01	66	18/4/2017 14:31	67	24/4/2017 9:01	65
29/3/2017 8:01	65	3/4/2017 14:01	67	10/4/2017 8:31	65	18/4/2017 15:01	68	24/4/2017 9:31	66
29/3/2017 8:31	66	3/4/2017 14:31	66	10/4/2017 9:01	66	18/4/2017 15:31	68	24/4/2017 10:01	68
29/3/2017 9:01	66	3/4/2017 15:01	67	10/4/2017 9:31	66	18/4/2017 16:01	67	24/4/2017 10:31	68
29/3/2017 9:31	66	3/4/2017 15:31	65	10/4/2017 10:01	67	18/4/2017 16:31	67	24/4/2017 11:01	68
29/3/2017 10:01	65	3/4/2017 16:01	66	10/4/2017 10:31	66	18/4/2017 17:01	66	24/4/2017 11:31	67
29/3/2017 10:31	66	3/4/2017 16:31	67	10/4/2017 11:01	67	18/4/2017 17:31	66	24/4/2017 12:01	67
29/3/2017 11:01	66	3/4/2017 17:01	67	10/4/2017 11:31	66	18/4/2017 18:01	66	24/4/2017 12:31	67
29/3/2017 11:31	66	3/4/2017 17:31	67	10/4/2017 12:01	66	18/4/2017 18:31	66	24/4/2017 13:01	68
29/3/2017 12:01	67	3/4/2017 18:01	66	10/4/2017 12:31	66	19/4/2017 7:01	66	24/4/2017 13:31	67
29/3/2017 12:31	67	3/4/2017 18:31	66	10/4/2017 13:01	66	19/4/2017 7:31	67	24/4/2017 14:01	68
29/3/2017 13:01	67	5/4/2017 7:01	66	10/4/2017 13:31	66	19/4/2017 8:01	67	24/4/2017 14:31	67
29/3/2017 13:31	67	5/4/2017 7:31	66	10/4/2017 14:01	67	19/4/2017 8:31	67	24/4/2017 15:01	67
29/3/2017 14:01	68	5/4/2017 8:01	66	10/4/2017 14:31	66	19/4/2017 9:01	69	24/4/2017 15:31	67
29/3/2017 14:31	68	5/4/2017 8:31	65	10/4/2017 15:01	66	19/4/2017 9:31	68	24/4/2017 16:01	68
29/3/2017 15:01	67	5/4/2017 9:01	66	10/4/2017 15:31	66	19/4/2017 10:01	67	24/4/2017 16:31	67
29/3/2017 15:31	67	5/4/2017 9:31	67	10/4/2017 16:01	66	19/4/2017 10:31	67	24/4/2017 17:01	67
29/3/2017 16:01	69	5/4/2017 10:01	67	10/4/2017 16:31	67	19/4/2017 11:01	67	24/4/2017 17:31	67
29/3/2017 16:31	68	5/4/2017 10:31	67	10/4/2017 17:01	66	19/4/2017 11:31	66	24/4/2017 18:01	67
29/3/2017 17:01	67	5/4/2017 11:01	67	10/4/2017 17:31	66	19/4/2017 12:01	65	24/4/2017 18:31	67
29/3/2017 17:31	67	5/4/2017 11:31	67	10/4/2017 18:01	66	19/4/2017 12:31	66	25/4/2017 7:01	66
29/3/2017 18:01	67	5/4/2017 12:01	66	10/4/2017 18:31	65	19/4/2017 13:01	66	25/4/2017 7:31	67
29/3/2017 18:31	63	5/4/2017 12:31	66	11/4/2017 7:01	66	19/4/2017 13:31	67	25/4/2017 8:01	65
30/3/2017 7:01	66	5/4/2017 13:01	67	11/4/2017 7:31	66	19/4/2017 14:01	66	25/4/2017 8:31	65
30/3/2017 7:31	66	5/4/2017 13:31	67	11/4/2017 8:01	65	19/4/2017 14:31	66	25/4/2017 9:01	66
30/3/2017 8:01	65	5/4/2017 14:01	67	11/4/2017 8:31	65	19/4/2017 15:01	66	25/4/2017 9:31	67
30/3/2017 8:31	65	5/4/2017 14:31	67	11/4/2017 9:01	66	19/4/2017 15:31	67	25/4/2017 10:01	68
30/3/2017 9:01	66	5/4/2017 15:01	67	11/4/2017 9:31	66	19/4/2017 16:01	67	25/4/2017 10:31	68
30/3/2017 9:31	66	5/4/2017 15:31	67	11/4/2017 10:01	67	19/4/2017 16:31	67	25/4/2017 11:01	68
30/3/2017 10:01	66	5/4/2017 16:01	67	11/4/2017 10:31	66	19/4/2017 17:01	66	25/4/2017 11:31	67
30/3/2017 10:31	66	5/4/2017 16:31	67	11/4/2017 11:01	66	19/4/2017 17:31	66	25/4/2017 12:01	66
30/3/2017 11:01	68	5/4/2017 17:01	66	11/4/2017 11:31	66	19/4/2017 18:01	66	25/4/2017 12:31	67
30/3/2017 11:31	67	5/4/2017 17:31	66	11/4/2017 12:01	66	19/4/2017 18:31	67	25/4/2017 13:01	67
30/3/2017 12:01	66	5/4/2017 18:01	66	11/4/2017 12:31	66	20/4/2017 7:01	68	25/4/2017 13:31	68
30/3/2017 12:31	67	5/4/2017 18:31	66	11/4/2017 13:01	66	20/4/2017 7:31	67	25/4/2017 14:01	67
30/3/2017 13:01	67	6/4/2017 7:01	66	11/4/2017 13:31	67	20/4/2017 8:01	67	25/4/2017 14:31	65
30/3/2017 13:31	68	6/4/2017 7:31	66	11/4/2017 14:01	67	20/4/2017 8:31	66	25/4/2017 15:01	66
30/3/2017 14:01	67	6/4/2017 8:01	66	11/4/2017 14:31	67	20/4/2017 9:01	66	25/4/2017 15:31	65
30/3/2017 14:31	67	6/4/2017 8:31	68	11/4/2017 15:01	67	20/4/2017 9:31	67	25/4/2017 16:01	66
30									

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
29/3/2017 19:01	63	31/3/2017 20:06	66	2/4/2017 9:11	66	2/4/2017 18:16	66	4/4/2017 7:21	64	4/4/2017 16:26	66
29/3/2017 19:06	63	31/3/2017 20:11	66	2/4/2017 9:16	66	2/4/2017 18:21	66	4/4/2017 7:26	64	4/4/2017 16:31	65
29/3/2017 19:11	65	31/3/2017 20:16	66	2/4/2017 9:21	66	2/4/2017 18:26	66	4/4/2017 7:31	64	4/4/2017 16:36	65
29/3/2017 19:16	66	31/3/2017 20:21	53	2/4/2017 9:26	66	2/4/2017 18:31	66	4/4/2017 7:36	64	4/4/2017 16:41	66
29/3/2017 19:21	66	31/3/2017 20:26	64	2/4/2017 9:31	66	2/4/2017 18:36	66	4/4/2017 7:41	65	4/4/2017 16:46	66
29/3/2017 19:26	66	31/3/2017 20:31	66	2/4/2017 9:36	66	2/4/2017 18:41	66	4/4/2017 7:46	65	4/4/2017 16:51	66
29/3/2017 19:31	65	31/3/2017 20:36	58	2/4/2017 9:41	66	2/4/2017 18:46	66	4/4/2017 7:51	64	4/4/2017 16:56	66
29/3/2017 19:36	66	31/3/2017 20:41	66	2/4/2017 9:46	66	2/4/2017 18:51	65	4/4/2017 7:56	66	4/4/2017 17:01	54
29/3/2017 19:41	66	31/3/2017 20:46	57	2/4/2017 9:51	58	2/4/2017 18:56	66	4/4/2017 8:01	65	4/4/2017 17:06	66
29/3/2017 19:46	66	31/3/2017 20:51	66	2/4/2017 9:56	66	2/4/2017 19:01	66	4/4/2017 8:06	64	4/4/2017 17:11	65
29/3/2017 19:51	56	31/3/2017 20:56	40	2/4/2017 10:01	65	2/4/2017 19:06	65	4/4/2017 8:11	65	4/4/2017 17:16	65
29/3/2017 19:56	66	31/3/2017 21:01	46	2/4/2017 10:06	65	2/4/2017 19:11	65	4/4/2017 8:16	66	4/4/2017 17:21	66
29/3/2017 20:01	66	31/3/2017 21:06	66	2/4/2017 10:11	66	2/4/2017 19:16	65	4/4/2017 8:21	64	4/4/2017 17:26	66
29/3/2017 20:06	65	31/3/2017 21:11	66	2/4/2017 10:16	66	2/4/2017 19:21	65	4/4/2017 8:26	65	4/4/2017 17:31	65
29/3/2017 20:11	66	31/3/2017 21:16	66	2/4/2017 10:21	65	2/4/2017 19:26	65	4/4/2017 8:31	65	4/4/2017 17:36	66
29/3/2017 20:16	66	31/3/2017 21:21	66	2/4/2017 10:26	66	2/4/2017 19:31	66	4/4/2017 8:36	66	4/4/2017 17:41	66
29/3/2017 20:21	61	31/3/2017 21:26	66	2/4/2017 10:31	66	2/4/2017 19:36	65	4/4/2017 8:41	65	4/4/2017 17:46	65
29/3/2017 20:26	65	31/3/2017 21:31	66	2/4/2017 10:36	66	2/4/2017 19:41	65	4/4/2017 8:46	66	4/4/2017 17:51	66
29/3/2017 20:31	65	31/3/2017 21:36	66	2/4/2017 10:41	66	2/4/2017 19:46	65	4/4/2017 8:51	65	4/4/2017 17:56	66
29/3/2017 20:36	65	31/3/2017 21:41	66	2/4/2017 10:46	66	2/4/2017 19:51	65	4/4/2017 8:56	65	4/4/2017 18:01	65
29/3/2017 20:41	65	31/3/2017 21:46	56	2/4/2017 10:51	66	2/4/2017 19:56	65	4/4/2017 9:01	65	4/4/2017 18:06	66
29/3/2017 20:46	65	31/3/2017 21:51	52	2/4/2017 10:56	66	2/4/2017 20:01	65	4/4/2017 9:06	65	4/4/2017 18:11	65
29/3/2017 20:51	65	31/3/2017 21:56	66	2/4/2017 11:01	66	2/4/2017 20:06	65	4/4/2017 9:11	66	4/4/2017 18:16	66
29/3/2017 20:56	65	31/3/2017 22:01	60	2/4/2017 11:06	66	2/4/2017 20:11	65	4/4/2017 9:16	65	4/4/2017 18:21	65
29/3/2017 21:01	65	31/3/2017 22:06	66	2/4/2017 11:11	66	2/4/2017 20:16	65	4/4/2017 9:21	65	4/4/2017 18:26	66
29/3/2017 21:06	65	31/3/2017 22:11	58	2/4/2017 11:16	66	2/4/2017 20:21	65	4/4/2017 9:26	66	4/4/2017 18:31	66
29/3/2017 21:11	66	31/3/2017 22:16	66	2/4/2017 11:21	66	2/4/2017 20:26	65	4/4/2017 9:31	65	4/4/2017 18:36	65
29/3/2017 21:16	65	31/3/2017 22:21	66	2/4/2017 11:26	66	2/4/2017 20:31	65	4/4/2017 9:36	65	4/4/2017 18:41	66
29/3/2017 21:21	65	31/3/2017 22:26	59	2/4/2017 11:31	66	2/4/2017 20:36	65	4/4/2017 9:41	58	4/4/2017 18:46	66
29/3/2017 21:26	65	31/3/2017 22:31	66	2/4/2017 11:36	66	2/4/2017 20:41	65	4/4/2017 9:46	66	4/4/2017 18:51	66
29/3/2017 21:31	65	31/3/2017 22:36	66	2/4/2017 11:41	66	2/4/2017 20:46	64	4/4/2017 9:51	65	4/4/2017 18:56	65
29/3/2017 21:36	64	31/3/2017 22:41	66	2/4/2017 11:46	52	2/4/2017 20:51	65	4/4/2017 9:56	66	4/4/2017 19:01	65
29/3/2017 21:41	66	31/3/2017 22:46	66	2/4/2017 11:51	66	2/4/2017 20:56	65	4/4/2017 10:01	66	4/4/2017 19:06	65
29/3/2017 21:46	66	31/3/2017 22:51	66	2/4/2017 11:56	66	2/4/2017 21:01	65	4/4/2017 10:06	59	4/4/2017 19:11	66
29/3/2017 21:51	65	31/3/2017 22:56	58	2/4/2017 12:01	66	2/4/2017 21:06	65	4/4/2017 10:11	65	4/4/2017 19:16	65
29/3/2017 21:56	65	1/4/2017 19:01	65	2/4/2017 12:06	66	2/4/2017 21:11	64	4/4/2017 10:16	65	4/4/2017 19:21	65
29/3/2017 22:01	65	1/4/2017 19:06	66	2/4/2017 12:11	66	2/4/2017 21:16	65	4/4/2017 10:21	65	4/4/2017 19:26	65
29/3/2017 22:06	65	1/4/2017 19:11	66	2/4/2017 12:16	66	2/4/2017 21:21	65	4/4/2017 10:26	66	4/4/2017 19:31	66
29/3/2017 22:11	65	1/4/2017 19:16	65	2/4/2017 12:21	66	2/4/2017 21:26	65	4/4/2017 10:31	66	4/4/2017 19:36	65
29/3/2017 22:16	65	1/4/2017 19:21	66	2/4/2017 12:26	65	2/4/2017 21:31	66	4/4/2017 10:36	66	4/4/2017 19:41	65
29/3/2017 22:21	65	1/4/2017 19:26	65	2/4/2017 12:31	65	2/4/2017 21:36	65	4/4/2017 10:41	65	4/4/2017 19:46	66
29/3/2017 22:26	65	1/4/2017 19:31	66	2/4/2017 12:36	65	2/4/2017 21:41	65	4/4/2017 10:46	66	4/4/2017 19:51	65
29/3/2017 22:31	65	1/4/2017 19:36	66	2/4/2017 12:41	66	2/4/2017 21:46	66	4/4/2017 10:51	66	4/4/2017 19:56	65
29/3/2017 22:36	65	1/4/2017 19:41	66	2/4/2017 12:46	66	2/4/2017 21:51	65	4/4/2017 10:56	66	4/4/2017 20:01	65
29/3/2017 22:41	65	1/4/2017 19:46	66	2/4/2017 12:51	66	2/4/2017 21:56	64	4/4/2017 11:01	66	4/4/2017 20:06	65
29/3/2017 22:46	65	1/4/2017 19:51	66	2/4/2017 12:56	66	2/4/2017 22:01	65	4/4/2017 11:06	65	4/4/2017 20:11	65
29/3/2017 22:51	65	1/4/2017 19:56	53	2/4/2017 13:01	65	2/4/2017 22:06	65	4/4/2017 11:11	65	4/4/2017 20:16	65
29/3/2017 22:56	64	1/4/2017 20:01	65	2/4/2017 13:06	66	2/4/2017 22:11	65	4/4/2017 11:16	66	4/4/2017 20:21	65
30/3/2017 19:01	53	1/4/2017 20:06	66	2/4/2017 13:11	66	2/4/2017 22:16	65	4/4/2017 11:21	65	4/4/2017 20:26	65
30/3/2017 19:06	55	1/4/2017 20:11	66	2/4/2017 13:16	65	2/4/2017 22:21	64	4/4/2017 11:26	65	4/4/2017 20:31	66
30/3/2017 19:11	66	1/4/2017 20:16	66	2/4/2017 13:21	55	2/4/2017 22:26	65	4/4/2017 11:31	65	4/4/2017 20:36	66
30/3/2017 19:16	66	1/4/2017 20:21	66	2/4/2017 13:26	66	2/4/2017 22:31	65	4/4/2017 11:36	65	4/4/2017 20:41	66
30/3/2017 19:21	66	1/4/2017 20:26	48	2/4/2017 13:31	66	2/4/2017 22:36	64	4/4/2017 11:41	65	4/4/2017 20:46	65
30/3/2017 19:26	66	1/4/2017 20:31	66	2/4/2017 13:36	65	2/4/2017 22:41	64	4/4/2017 11:46	65	4/4/2017 20:51	65
30/3/2017 19:31	66	1/4/2017 20:36	66	2/4/2017 13:41	65	2/4/2017 22:46	65	4/4/2017 11:51	66	4/4/2017 20:56	66
30/3/2017 19:36	66	1/4/2017 20:41	66	2/4/2017 13:46	65	2/4/2017 22:51	65	4/4/2017 11:56	66	4/4/2017 21:01	65
30/3/2017 19:41	66	1/4/2017 20:46	66	2/4/2017 13:51	65	2/4/2017 22:56	64	4/4/2017 12:01	65	4/4/2017 21:06	65
30/3/2017 19:46	66	1/4/2017 20:51	65	2/4/2017 13:56	66	3/4/2017 19:01	66	4/4/2017 12:06	65	4/4/2017 21:11	65
30/3/2017 19:51	65	1/4/2017 20:56	65	2/4/2017 14:01	65	3/4/2017 19:06	66	4/4/2017 12:11	65	4/4/2017 21:16	65
30/3/2017 19:56	65	1/4/2017 21:01	66	2/4/2017 14:06	66	3/4/2017 19:11	66	4/4/2017 12:16	65	4/4/2017 21:21	65
30/3/2017 20:01	66	1/4/2017 21:06	65	2/4/2017 14:11	65	3/4/2017 19:16	66	4/4/2017 12:21	62	4/4/2017 21:26	65
30/3/2017 20:06	66	1/4/2017 21:11	65	2/4/2017 14:16	66	3/4/2017 19:21	65	4/4/2017 12:26	65	4/4/2017 21:31	65
30/3/2017 20:11	65	1/4/2017 21:16	65	2/4/2017 14:21	65	3/4/2017 19:26	66	4/4/2017 12:31	65	4/4/2017 21:36	65
30/3/2017 20:16	65	1/4/2017 21:21	65	2/4/2017 14:26	65	3/4/2017 19:31	66	4/4/2017 12:36	65	4/4/2017 21:41	65
30/3/2017 20:21	65	1/4/2017 21:26	66	2/4/2017 14:31	65	3/4/2017 19:36	66	4/4/2017 12:41	66	4/4/2017 21:46	65
30/3/2017 20:26	66	1/4/2017 21:31	65	2/4/2017 14:36	65	3/4/2017 19:41	66	4/4/2017 12:46	66	4/4/2017 21:51	65
30/3/2017 20:31	66	1/4/2017 21:36	65	2/4/2017 14:41	66	3/4/2017 19:46	66	4/4/2017 12:51	65	4/4/2017 21:56	65
30/3/2017 20:36	66	1/4/2017 21:41	65	2/4/2017 14:46	65	3/4/2017 19:51	66	4/4/2017 12:56	62	4/4/2017 22:01	65
30/3/2017 20:41	66	1/4/2017 21:46	65	2/4/2017 14:51	65	3/4/2017 19:56	66	4/4/2017 13:01	66	4/4/2017 22:06	65
30/3/2017 20:46	66	1/4/2017 21:51	66	2/4/2017 14:56	65	3/4/2017 20:01	66	4/4/2017 13:06	65	4/4/2017 22:11	64
30/3/2017 20:51	65	1/4/2017 21:56	65	2/4/2017 15:01	66	3/4/2017 20:06	65	4/4/2017 13:11	65	4/4/2017 22:16	65
30/3/2017 20:56	65	1/4/2017 22:01	65	2/4/2017 15:06	65	3/4/2017 20:11	66	4/4/2017 13:16	66	4/4/2017 22:21	64
30/3/2017 21:01	65	1/4/2017 22:06	65	2/4/2017 15:11	65	3/4/2017 20:16	66	4/4/2017 13:21	66	4/4/2017 22:26	63
30/3/2017 21:06	65	1/4/2017 22:11	65	2/4/2017 15:16	65	3/4/2017 20:21	65	4/4/2017 13:26	55	4/4/2017 22:31	64
30/3/2017 21:11	66	1/4/2017 22:16	65	2/4/2017 15:21	65	3/4/2017 20:26	66	4/4/2017 13:31	66	4/4/2017 22:36	64
30/3/2017 21:16	65	1/4/2017 22:21	65	2/4/2017 15:26	65						

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
5/4/2017 21:31	65	7/4/2017 22:36	65	9/4/2017 11:41	65	9/4/2017 20:46	64	11/4/2017 21:51	64	13/4/2017 22:56	66
5/4/2017 21:36	65	7/4/2017 22:41	65	9/4/2017 11:46	66	9/4/2017 20:51	64	11/4/2017 21:56	64	14/4/2017 7:01	65
5/4/2017 21:41	63	7/4/2017 22:46	65	9/4/2017 11:51	65	9/4/2017 20:56	64	11/4/2017 22:01	64	14/4/2017 7:06	65
5/4/2017 21:46	65	7/4/2017 22:51	65	9/4/2017 11:56	65	9/4/2017 21:01	64	11/4/2017 22:06	64	14/4/2017 7:11	64
5/4/2017 21:51	66	7/4/2017 22:56	65	9/4/2017 12:01	53	9/4/2017 21:06	64	11/4/2017 22:11	64	14/4/2017 7:16	65
5/4/2017 21:56	66	8/4/2017 19:01	66	9/4/2017 12:06	65	9/4/2017 21:11	64	11/4/2017 22:16	65	14/4/2017 7:21	65
5/4/2017 22:01	64	8/4/2017 19:06	65	9/4/2017 12:11	65	9/4/2017 21:16	64	11/4/2017 22:21	65	14/4/2017 7:26	65
5/4/2017 22:06	65	8/4/2017 19:11	66	9/4/2017 12:16	66	9/4/2017 21:21	64	11/4/2017 22:26	65	14/4/2017 7:31	65
5/4/2017 22:11	65	8/4/2017 19:16	66	9/4/2017 12:21	65	9/4/2017 21:26	64	11/4/2017 22:31	64	14/4/2017 7:36	65
5/4/2017 22:16	65	8/4/2017 19:21	65	9/4/2017 12:26	65	9/4/2017 21:31	64	11/4/2017 22:36	64	14/4/2017 7:41	65
5/4/2017 22:21	65	8/4/2017 19:26	65	9/4/2017 12:31	65	9/4/2017 21:36	64	11/4/2017 22:41	64	14/4/2017 7:46	66
5/4/2017 22:26	65	8/4/2017 19:31	65	9/4/2017 12:36	65	9/4/2017 21:41	64	11/4/2017 22:46	64	14/4/2017 7:51	65
5/4/2017 22:31	66	8/4/2017 19:36	62	9/4/2017 12:41	66	9/4/2017 21:46	64	11/4/2017 22:51	65	14/4/2017 7:56	65
5/4/2017 22:36	65	8/4/2017 19:41	66	9/4/2017 12:46	66	9/4/2017 21:51	64	11/4/2017 22:56	64	14/4/2017 8:01	65
5/4/2017 22:41	66	8/4/2017 19:46	65	9/4/2017 12:51	65	9/4/2017 21:56	64	12/4/2017 19:01	54	14/4/2017 8:06	66
5/4/2017 22:46	64	8/4/2017 19:51	65	9/4/2017 12:56	65	9/4/2017 22:01	64	12/4/2017 19:06	59	14/4/2017 8:11	66
5/4/2017 22:51	65	8/4/2017 19:56	65	9/4/2017 13:01	66	9/4/2017 22:06	64	12/4/2017 19:11	58	14/4/2017 8:16	66
5/4/2017 22:56	65	8/4/2017 20:01	65	9/4/2017 13:06	65	9/4/2017 22:11	65	12/4/2017 19:16	40	14/4/2017 8:21	58
6/4/2017 19:01	66	8/4/2017 20:06	65	9/4/2017 13:11	65	9/4/2017 22:16	64	12/4/2017 19:21	50	14/4/2017 8:26	66
6/4/2017 19:06	66	8/4/2017 20:11	64	9/4/2017 13:16	65	9/4/2017 22:21	64	12/4/2017 19:26	61	14/4/2017 8:31	66
6/4/2017 19:11	65	8/4/2017 20:16	65	9/4/2017 13:21	66	9/4/2017 22:26	64	12/4/2017 19:31	66	14/4/2017 8:36	51
6/4/2017 19:16	65	8/4/2017 20:21	66	9/4/2017 13:26	65	9/4/2017 22:31	64	12/4/2017 19:36	66	14/4/2017 8:41	66
6/4/2017 19:21	66	8/4/2017 20:26	65	9/4/2017 13:31	65	9/4/2017 22:36	63	12/4/2017 19:41	66	14/4/2017 8:46	66
6/4/2017 19:26	66	8/4/2017 20:31	65	9/4/2017 13:36	66	9/4/2017 22:41	64	12/4/2017 19:46	66	14/4/2017 8:51	66
6/4/2017 19:31	66	8/4/2017 20:36	66	9/4/2017 13:41	65	9/4/2017 22:46	63	12/4/2017 19:51	66	14/4/2017 8:56	66
6/4/2017 19:36	65	8/4/2017 20:41	65	9/4/2017 13:46	65	9/4/2017 22:51	64	12/4/2017 19:56	54	14/4/2017 9:01	67
6/4/2017 19:41	66	8/4/2017 20:46	64	9/4/2017 13:51	65	9/4/2017 22:56	65	12/4/2017 20:01	66	14/4/2017 9:06	43
6/4/2017 19:46	66	8/4/2017 20:51	65	9/4/2017 13:56	66	10/4/2017 19:01	65	12/4/2017 20:06	65	14/4/2017 9:11	66
6/4/2017 19:51	66	8/4/2017 20:56	65	9/4/2017 14:01	65	10/4/2017 19:06	65	12/4/2017 20:11	66	14/4/2017 9:16	66
6/4/2017 19:56	65	8/4/2017 21:01	65	9/4/2017 14:06	65	10/4/2017 19:11	65	12/4/2017 20:16	61	14/4/2017 9:21	51
6/4/2017 20:01	66	8/4/2017 21:06	65	9/4/2017 14:11	65	10/4/2017 19:16	65	12/4/2017 20:21	66	14/4/2017 9:26	66
6/4/2017 20:06	65	8/4/2017 21:11	64	9/4/2017 14:16	65	10/4/2017 19:21	65	12/4/2017 20:26	66	14/4/2017 9:31	66
6/4/2017 20:11	65	8/4/2017 21:16	66	9/4/2017 14:21	65	10/4/2017 19:26	65	12/4/2017 20:31	66	14/4/2017 9:36	66
6/4/2017 20:16	65	8/4/2017 21:21	65	9/4/2017 14:26	65	10/4/2017 19:31	65	12/4/2017 20:36	56	14/4/2017 9:41	66
6/4/2017 20:21	65	8/4/2017 21:26	65	9/4/2017 14:31	65	10/4/2017 19:36	49	12/4/2017 20:41	66	14/4/2017 9:46	66
6/4/2017 20:26	65	8/4/2017 21:31	65	9/4/2017 14:36	64	10/4/2017 19:41	65	12/4/2017 20:46	66	14/4/2017 9:51	66
6/4/2017 20:31	54	8/4/2017 21:36	65	9/4/2017 14:41	66	10/4/2017 19:46	65	12/4/2017 20:51	66	14/4/2017 9:56	66
6/4/2017 20:36	64	8/4/2017 21:41	65	9/4/2017 14:46	65	10/4/2017 19:51	65	12/4/2017 20:56	48	14/4/2017 10:01	57
6/4/2017 20:41	65	8/4/2017 21:46	65	9/4/2017 14:51	65	10/4/2017 19:56	65	12/4/2017 21:01	66	14/4/2017 10:06	66
6/4/2017 20:46	64	8/4/2017 21:51	65	9/4/2017 14:56	65	10/4/2017 20:01	65	12/4/2017 21:06	66	14/4/2017 10:11	59
6/4/2017 20:51	65	8/4/2017 21:56	65	9/4/2017 15:01	65	10/4/2017 20:06	65	12/4/2017 21:11	66	14/4/2017 10:16	66
6/4/2017 20:56	65	8/4/2017 22:01	66	9/4/2017 15:06	65	10/4/2017 20:11	56	12/4/2017 21:16	66	14/4/2017 10:21	66
6/4/2017 21:01	65	8/4/2017 22:06	65	9/4/2017 15:11	65	10/4/2017 20:16	65	12/4/2017 21:21	66	14/4/2017 10:26	66
6/4/2017 21:06	65	8/4/2017 22:11	65	9/4/2017 15:16	65	10/4/2017 20:21	66	12/4/2017 21:26	66	14/4/2017 10:31	66
6/4/2017 21:11	64	8/4/2017 22:16	65	9/4/2017 15:21	66	10/4/2017 20:26	64	12/4/2017 21:31	65	14/4/2017 10:36	66
6/4/2017 21:16	64	8/4/2017 22:21	65	9/4/2017 15:26	65	10/4/2017 20:31	64	12/4/2017 21:36	66	14/4/2017 10:41	58
6/4/2017 21:21	64	8/4/2017 22:26	65	9/4/2017 15:31	65	10/4/2017 20:36	64	12/4/2017 21:41	65	14/4/2017 10:46	57
6/4/2017 21:26	65	8/4/2017 22:31	65	9/4/2017 15:36	66	10/4/2017 20:41	64	12/4/2017 21:46	65	14/4/2017 10:51	66
6/4/2017 21:31	64	8/4/2017 22:36	65	9/4/2017 15:41	65	10/4/2017 20:46	65	12/4/2017 21:51	66	14/4/2017 10:56	53
6/4/2017 21:36	66	8/4/2017 22:41	65	9/4/2017 15:46	65	10/4/2017 20:51	65	12/4/2017 21:56	66	14/4/2017 11:01	66
6/4/2017 21:41	64	8/4/2017 22:46	65	9/4/2017 15:51	65	10/4/2017 20:56	65	12/4/2017 22:01	66	14/4/2017 11:06	66
6/4/2017 21:46	65	8/4/2017 22:51	66	9/4/2017 15:56	66	10/4/2017 21:01	64	12/4/2017 22:06	66	14/4/2017 11:11	66
6/4/2017 21:51	65	8/4/2017 22:56	66	9/4/2017 16:01	65	10/4/2017 21:06	64	12/4/2017 22:11	66	14/4/2017 11:16	66
6/4/2017 21:56	65	9/4/2017 7:01	64	9/4/2017 16:06	65	10/4/2017 21:11	64	12/4/2017 22:16	66	14/4/2017 11:21	66
6/4/2017 22:01	65	9/4/2017 7:06	65	9/4/2017 16:11	66	10/4/2017 21:16	65	12/4/2017 22:21	66	14/4/2017 11:26	66
6/4/2017 22:06	65	9/4/2017 7:11	63	9/4/2017 16:16	65	10/4/2017 21:21	65	12/4/2017 22:26	66	14/4/2017 11:31	66
6/4/2017 22:11	65	9/4/2017 7:16	64	9/4/2017 16:21	65	10/4/2017 21:26	64	12/4/2017 22:31	66	14/4/2017 11:36	66
6/4/2017 22:16	65	9/4/2017 7:21	65	9/4/2017 16:26	66	10/4/2017 21:31	64	12/4/2017 22:36	66	14/4/2017 11:41	66
6/4/2017 22:21	65	9/4/2017 7:26	66	9/4/2017 16:31	65	10/4/2017 21:36	64	12/4/2017 22:41	66	14/4/2017 11:46	66
6/4/2017 22:26	65	9/4/2017 7:31	64	9/4/2017 16:36	65	10/4/2017 21:41	64	12/4/2017 22:46	65	14/4/2017 11:51	66
6/4/2017 22:31	65	9/4/2017 7:36	64	9/4/2017 16:41	65	10/4/2017 21:46	64	12/4/2017 22:51	66	14/4/2017 11:56	66
6/4/2017 22:36	65	9/4/2017 7:41	64	9/4/2017 16:46	65	10/4/2017 21:51	64	12/4/2017 22:56	65	14/4/2017 12:01	66
6/4/2017 22:41	65	9/4/2017 7:46	65	9/4/2017 16:51	65	10/4/2017 21:56	64	13/4/2017 19:01	64	14/4/2017 12:06	66
6/4/2017 22:46	65	9/4/2017 7:51	65	9/4/2017 16:56	64	10/4/2017 22:01	64	13/4/2017 19:06	64	14/4/2017 12:11	65
6/4/2017 22:51	65	9/4/2017 7:56	65	9/4/2017 17:01	65	10/4/2017 22:06	64	13/4/2017 19:11	64	14/4/2017 12:16	66
6/4/2017 22:56	65	9/4/2017 8:01	65	9/4/2017 17:06	64	10/4/2017 22:11	65	13/4/2017 19:16	65	14/4/2017 12:21	66
7/4/2017 19:01	66	9/4/2017 8:06	64	9/4/2017 17:11	65	10/4/2017 22:16	64	13/4/2017 19:21	66	14/4/2017 12:26	66
7/4/2017 19:06	66	9/4/2017 8:11	65	9/4/2017 17:16	65	10/4/2017 22:21	64	13/4/2017 19:26	66	14/4/2017 12:31	66
7/4/2017 19:11	66	9/4/2017 8:16	65	9/4/2017 17:21	65	10/4/2017 22:26	65	13/4/2017 19:31	66	14/4/2017 12:36	66
7/4/2017 19:16	66	9/4/2017 8:21	65	9/4/2017 17:26	65	10/4/2017 22:31	64	13/4/2017 19:36	66	14/4/2017 12:41	66
7/4/2017 19:21	66	9/4/2017 8:26	65	9/4/2017 17:31	65	10/4/2017 22:36	64	13/4/2017 19:41	58	14/4/2017 12:46	66
7/4/2017 19:26	67	9/4/2017 8:31	65	9/4/2017 17:36	65	10/4/2017 22:41	64	13/4/2017 19:46	66	14/4/2017 12:51	66
7/4/2017 19:31	66	9/4/2017 8:36	65	9/4/2017 17:41	65	10/4/2017 22:46	63	13/4/2017 19:51	45	14/4/2017 12:56	66
7/4/2017 19:36	66	9/4/2017 8:41	66	9/4/2017 17:46	65	10/4/2017 22:51	63	13/4/2017 19:56	66	14/4/2017 13:01	66
7/4/2017 19:41	65	9/4/2017 8:46	65	9/4/2017 17:51	65	10/4/2017 22:56	63	13/4/2017 20:01	66	14/4/2017 13:06	66
7/											

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)					
14/4/2017 16:01	64	15/4/2017 9:06	66	15/4/2017 18:11	66	16/4/2017 11:16	65
14/4/2017 16:06	66	15/4/2017 9:11	66	15/4/2017 18:16	66	16/4/2017 11:21	66
14/4/2017 16:11	66	15/4/2017 9:16	66	15/4/2017 18:21	66	16/4/2017 11:26	66
14/4/2017 16:16	66	15/4/2017 9:21	65	15/4/2017 18:26	66	16/4/2017 11:31	65
14/4/2017 16:21	60	15/4/2017 9:26	65	15/4/2017 18:31	66	16/4/2017 11:36	51
14/4/2017 16:26	66	15/4/2017 9:31	66	15/4/2017 18:36	66	16/4/2017 11:41	56
14/4/2017 16:31	66	15/4/2017 9:36	61	15/4/2017 18:41	66	16/4/2017 11:46	50
14/4/2017 16:36	66	15/4/2017 9:41	66	15/4/2017 18:46	66	16/4/2017 11:51	66
14/4/2017 16:41	66	15/4/2017 9:46	66	15/4/2017 18:51	65	16/4/2017 11:56	52
14/4/2017 16:46	66	15/4/2017 9:51	66	15/4/2017 18:56	66	16/4/2017 12:01	66
14/4/2017 16:51	66	15/4/2017 9:56	66	15/4/2017 19:01	66	16/4/2017 12:06	66
14/4/2017 16:56	66	15/4/2017 10:01	49	15/4/2017 19:06	60	16/4/2017 12:11	66
14/4/2017 17:01	66	15/4/2017 10:06	66	15/4/2017 19:11	65	16/4/2017 12:16	66
14/4/2017 17:06	66	15/4/2017 10:11	66	15/4/2017 19:16	66	16/4/2017 12:21	66
14/4/2017 17:11	66	15/4/2017 10:16	50	15/4/2017 19:21	66	16/4/2017 12:26	48
14/4/2017 17:16	65	15/4/2017 10:21	66	15/4/2017 19:26	65	16/4/2017 12:31	66
14/4/2017 17:21	66	15/4/2017 10:26	66	15/4/2017 19:31	65	16/4/2017 12:36	66
14/4/2017 17:26	66	15/4/2017 10:31	66	15/4/2017 19:36	66	16/4/2017 12:41	66
14/4/2017 17:31	66	15/4/2017 10:36	66	15/4/2017 19:41	65	16/4/2017 12:46	66
14/4/2017 17:36	66	15/4/2017 10:41	53	15/4/2017 19:46	65	16/4/2017 12:51	66
14/4/2017 17:41	66	15/4/2017 10:46	66	15/4/2017 19:51	65	16/4/2017 12:56	66
14/4/2017 17:46	65	15/4/2017 10:51	66	15/4/2017 19:56	65	16/4/2017 13:01	66
14/4/2017 17:51	66	15/4/2017 10:56	55	15/4/2017 20:01	65	16/4/2017 13:06	65
14/4/2017 17:56	66	15/4/2017 11:01	53	15/4/2017 20:06	45	16/4/2017 13:11	66
14/4/2017 18:01	66	15/4/2017 11:06	66	15/4/2017 20:11	65	16/4/2017 13:16	65
14/4/2017 18:06	66	15/4/2017 11:11	66	15/4/2017 20:16	66	16/4/2017 13:21	66
14/4/2017 18:11	65	15/4/2017 11:16	66	15/4/2017 20:21	65	16/4/2017 13:26	66
14/4/2017 18:16	66	15/4/2017 11:21	43	15/4/2017 20:26	65	16/4/2017 13:31	65
14/4/2017 18:21	65	15/4/2017 11:26	59	15/4/2017 20:31	66	16/4/2017 13:36	65
14/4/2017 18:26	66	15/4/2017 11:31	66	15/4/2017 20:36	66	16/4/2017 13:41	65
14/4/2017 18:31	66	15/4/2017 11:36	66	15/4/2017 20:41	65	16/4/2017 13:46	66
14/4/2017 18:36	65	15/4/2017 11:41	66	15/4/2017 20:46	65	16/4/2017 13:51	65
14/4/2017 18:41	66	15/4/2017 11:46	66	15/4/2017 20:51	65	16/4/2017 13:56	65
14/4/2017 18:46	66	15/4/2017 11:51	66	15/4/2017 20:56	64	16/4/2017 14:01	66
14/4/2017 18:51	65	15/4/2017 11:56	66	15/4/2017 21:01	65	16/4/2017 14:06	66
14/4/2017 18:56	66	15/4/2017 12:01	66	15/4/2017 21:06	65	16/4/2017 14:11	65
14/4/2017 19:01	66	15/4/2017 12:06	56	15/4/2017 21:11	65	16/4/2017 14:16	66
14/4/2017 19:06	66	15/4/2017 12:11	66	15/4/2017 21:16	65	16/4/2017 14:21	65
14/4/2017 19:11	66	15/4/2017 12:16	66	15/4/2017 21:21	65	16/4/2017 14:26	65
14/4/2017 19:16	65	15/4/2017 12:21	66	15/4/2017 21:26	66	16/4/2017 14:31	66
14/4/2017 19:21	65	15/4/2017 12:26	66	15/4/2017 21:31	65	16/4/2017 14:36	70
14/4/2017 19:26	65	15/4/2017 12:31	66	15/4/2017 21:36	65	16/4/2017 14:41	65
14/4/2017 19:31	66	15/4/2017 12:36	66	15/4/2017 21:41	65	16/4/2017 14:46	66
14/4/2017 19:36	66	15/4/2017 12:41	66	15/4/2017 21:46	64	16/4/2017 14:51	66
14/4/2017 19:41	66	15/4/2017 12:46	56	15/4/2017 21:51	65	16/4/2017 14:56	66
14/4/2017 19:46	66	15/4/2017 12:51	66	15/4/2017 21:56	66	16/4/2017 15:01	66
14/4/2017 19:51	66	15/4/2017 12:56	66	15/4/2017 22:01	65	16/4/2017 15:06	65
14/4/2017 19:56	66	15/4/2017 13:01	66	15/4/2017 22:06	65	16/4/2017 15:11	66
14/4/2017 20:01	65	15/4/2017 13:06	66	15/4/2017 22:11	65	16/4/2017 15:16	65
14/4/2017 20:06	65	15/4/2017 13:11	65	15/4/2017 22:16	65	16/4/2017 15:21	66
14/4/2017 20:11	65	15/4/2017 13:16	66	15/4/2017 22:21	65	16/4/2017 15:26	66
14/4/2017 20:16	65	15/4/2017 13:21	66	15/4/2017 22:26	65	16/4/2017 15:31	65
14/4/2017 20:21	65	15/4/2017 13:26	66	15/4/2017 22:31	66	16/4/2017 15:36	66
14/4/2017 20:26	65	15/4/2017 13:31	66	15/4/2017 22:36	65	16/4/2017 15:41	65
14/4/2017 20:31	65	15/4/2017 13:36	51	15/4/2017 22:41	65	16/4/2017 15:46	65
14/4/2017 20:36	66	15/4/2017 13:41	66	15/4/2017 22:46	65	16/4/2017 15:51	66
14/4/2017 20:41	66	15/4/2017 13:46	65	15/4/2017 22:51	65	16/4/2017 15:56	65
14/4/2017 20:46	65	15/4/2017 13:51	66	15/4/2017 22:56	65	16/4/2017 16:01	66
14/4/2017 20:51	65	15/4/2017 13:56	66	16/4/2017 7:01	63	16/4/2017 16:06	65
14/4/2017 20:56	65	15/4/2017 14:01	66	16/4/2017 7:06	65	16/4/2017 16:11	56
14/4/2017 21:01	66	15/4/2017 14:06	66	16/4/2017 7:11	63	16/4/2017 16:16	65
14/4/2017 21:06	65	15/4/2017 14:11	66	16/4/2017 7:16	62	16/4/2017 16:21	66
14/4/2017 21:11	65	15/4/2017 14:16	66	16/4/2017 7:21	64	16/4/2017 16:26	66
14/4/2017 21:16	65	15/4/2017 14:21	66	16/4/2017 7:26	66	16/4/2017 16:31	66
14/4/2017 21:21	65	15/4/2017 14:26	66	16/4/2017 7:31	63	16/4/2017 16:36	65
14/4/2017 21:26	65	15/4/2017 14:31	66	16/4/2017 7:36	65	16/4/2017 16:41	66
14/4/2017 21:31	66	15/4/2017 14:36	66	16/4/2017 7:41	64	16/4/2017 16:46	66
14/4/2017 21:36	65	15/4/2017 14:41	66	16/4/2017 7:46	64	16/4/2017 16:51	65
14/4/2017 21:41	66	15/4/2017 14:46	66	16/4/2017 7:51	65	16/4/2017 16:56	65
14/4/2017 21:46	65	15/4/2017 14:51	66	16/4/2017 7:56	64	16/4/2017 17:01	66
14/4/2017 21:51	64	15/4/2017 14:56	66	16/4/2017 8:01	65	16/4/2017 17:06	66
14/4/2017 21:56	65	15/4/2017 15:01	65	16/4/2017 8:06	65	16/4/2017 17:11	65
14/4/2017 22:01	50	15/4/2017 15:06	66	16/4/2017 8:11	65	16/4/2017 17:16	66
14/4/2017 22:06	65	15/4/2017 15:11	66	16/4/2017 8:16	65	16/4/2017 17:21	65
14/4/2017 22:11	66	15/4/2017 15:16	66	16/4/2017 8:21	64	16/4/2017 17:26	65
14/4/2017 22:16	66	15/4/2017 15:21	66	16/4/2017 8:26	65	16/4/2017 17:31	65
14/4/2017 22:21	65	15/4/2017 15:26	66	16/4/2017 8:31	65	16/4/2017 17:36	65
14/4/2017 22:26	65	15/4/2017 15:31	66	16/4/2017 8:36	64	16/4/2017 17:41	65
14/4/2017 22:31	65	15/4/2017 15:36	66	16/4/2017 8:41	64	16/4/2017 17:46	65
14/4/2017 22:36	65	15/4/2017 15:41	66	16/4/2017 8:46	65	16/4/2017 17:51	66
14/4/2017 22:41	65	15/4/2017 15:46	52	16/4/2017 8:51	66	16/4/2017 17:56	66
14/4/2017 22:46	65	15/4/2017 15:51	66	16/4/2017 8:56	65	16/4/2017 18:01	65
14/4/2017 22:51	64	15/4/2017 15:56	55	16/4/2017 9:01	65	16/4/2017 18:06	66
14/4/2017 22:56	65	15/4/2017 16:01	66	16/4/2017 9:06	66	16/4/2017 18:11	66
15/4/2017 7:01	63	15/4/2017 16:06	65	16/4/2017 9:11	65	16/4/2017 18:16	66
15/4/2017 7:06	64	15/4/2017 16:11	66	16/4/2017 9:16	65	16/4/2017 18:21	66
15/4/2017 7:11	65	15/4/2017 16:16	66	16/4/2017 9:21	66	16/4/2017 18:26	65
15/4/2017 7:16	65	15/4/2017 16:21	66	16/4/2017 9:26	66	16/4/2017 18:31	66
15/4/2017 7:21	65	15/4/2017 16:26	66	16/4/2017 9:31	66	16/4/2017 18:36	65
15/4/2017 7:26	64	15/4/2017 16:31	66	16/4/2017 9:36	65	16/4/2017 18:41	65
15/4/2017 7:31	64	15/4/2017 16:36	66	16/4/2017 9:41	49	16/4/2017 18:46	65
15/4/2017 7:36	64	15/4/2017 16:41	66	16/4/2017 9:46	66	16/4/2017 18:51	65
15/4/2017 7:41	65	15/4/2017 16:46	66	16/4/2017 9:51	66	16/4/2017 18:56	65
15/4/2017 7:46	65	15/4/2017 16:51	66	16/4/2017 9:56	65	16/4/2017 19:01	66
15/4/2017 7:51	64	15/4/2017 16:56	66	16/4/2017 10:01	66	16/4/2017 19:06	65
15/4/2017 7:56	65	15/4/2017 17:01	66	16/4/2017 10:06	66	16/4/2017 19:11	65
15/4/2017 8:01	65	15/4/2017 17:06	66	16/4/2017 10:11	65	16/4/2017 19:16	65
15/4/2017 8:06	65	15/4/2017 17:11	66	16/4/2017 10:16	66	16/4/2017 19:21	65
15/4/2017 8:11	65	15/4/2017 17:16	66	16/4/2017 10:21	65	16/4/2017 19:26	65
15/4/2017 8:16	65	15/4/2017 17:21	66	16/4/2017 10:26	66	16/4/2017 19:31	65
15/4/2017 8:21	64	15/4/2017 17:26	66	16/4/2017 10:31	65	16/4/2017 19:36	65
15/4/2017 8:26	65	15/4/2017 17:31	66	16/4/2017 10:36	66	16/4/2017 19:41	65
15/4/2017 8:31	65	15/4/2017 17:36	66	16/4/2017 10:41	65	16/4/2017 19:46	65
15/4/2017 8:36	66	15/4/2017 17:41	66	16/4/2017 10:46	66	16/4/2017 19:51	65
15/4/2017 8:41	65	15/4/2017 17:46	66	16/4/2017 10:51	66	16/4/2017 19:56	66
15/4/2017 8:46	66	15/4/2017 17:51	66	16/4/2017 10:56	66	16/4/2017 20:01	65
15/4/2017 8:51	66	15/4/2017 17:56	66	16/4/2017 11:01	66	16/4/2017 20:06	65
15/4/2017 8:56	66	15/4/2017 18:01	55	16/4/2017 11:06	63	16/4/2017 20:11	65
15/4/2017 9:01	66	15/4/2017 18:06	66	16/4/2017 11:11	66	16/4/2017 20:16	65

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
17/4/2017 22:31	64	20/4/2017 19:36	66	22/4/2017 20:41	65	23/4/2017 13:46	66	23/4/2017 22:51	65	26/4/2017 19:56	56
17/4/2017 22:36	64	20/4/2017 19:41	66	22/4/2017 20:46	65	23/4/2017 13:51	55	23/4/2017 22:56	64	26/4/2017 20:01	65
17/4/2017 22:41	65	20/4/2017 19:46	59	22/4/2017 20:51	65	23/4/2017 13:56	66	24/4/2017 19:01	66	26/4/2017 20:06	66
17/4/2017 22:46	64	20/4/2017 19:51	66	22/4/2017 20:56	66	23/4/2017 14:01	66	24/4/2017 19:06	66	26/4/2017 20:11	66
17/4/2017 22:51	65	20/4/2017 19:56	66	22/4/2017 21:01	66	23/4/2017 14:06	66	24/4/2017 19:11	66	26/4/2017 20:16	66
17/4/2017 22:56	64	20/4/2017 20:01	66	22/4/2017 21:06	66	23/4/2017 14:11	66	24/4/2017 19:16	66	26/4/2017 20:21	66
18/4/2017 19:01	66	20/4/2017 20:06	66	22/4/2017 21:11	65	23/4/2017 14:16	66	24/4/2017 19:21	66	26/4/2017 20:26	66
18/4/2017 19:06	65	20/4/2017 20:11	66	22/4/2017 21:16	66	23/4/2017 14:21	66	24/4/2017 19:26	66	26/4/2017 20:31	66
18/4/2017 19:11	65	20/4/2017 20:16	56	22/4/2017 21:21	65	23/4/2017 14:26	48	24/4/2017 19:31	66	26/4/2017 20:36	52
18/4/2017 19:16	65	20/4/2017 20:21	66	22/4/2017 21:26	66	23/4/2017 14:31	66	24/4/2017 19:36	66	26/4/2017 20:41	66
18/4/2017 19:21	65	20/4/2017 20:26	66	22/4/2017 21:31	65	23/4/2017 14:36	66	24/4/2017 19:41	66	26/4/2017 20:46	66
18/4/2017 19:26	65	20/4/2017 20:31	66	22/4/2017 21:36	66	23/4/2017 14:41	66	24/4/2017 19:46	50	26/4/2017 20:51	65
18/4/2017 19:31	65	20/4/2017 20:36	66	22/4/2017 21:41	66	23/4/2017 14:46	56	24/4/2017 19:51	66	26/4/2017 20:56	66
18/4/2017 19:36	66	20/4/2017 20:41	66	22/4/2017 21:46	66	23/4/2017 14:51	66	24/4/2017 19:56	49	26/4/2017 21:01	66
18/4/2017 19:41	66	20/4/2017 20:46	66	22/4/2017 21:51	66	23/4/2017 14:56	66	24/4/2017 20:01	66	26/4/2017 21:06	66
18/4/2017 19:46	65	20/4/2017 20:51	66	22/4/2017 21:56	65	23/4/2017 15:01	66	24/4/2017 20:06	66	26/4/2017 21:11	66
18/4/2017 19:51	65	20/4/2017 20:56	65	22/4/2017 22:01	66	23/4/2017 15:06	66	24/4/2017 20:11	66	26/4/2017 21:16	66
18/4/2017 19:56	65	20/4/2017 21:01	66	22/4/2017 22:06	65	23/4/2017 15:11	66	24/4/2017 20:16	66	26/4/2017 21:21	65
18/4/2017 20:01	65	20/4/2017 21:06	65	22/4/2017 22:11	66	23/4/2017 15:16	66	24/4/2017 20:21	66	26/4/2017 21:26	65
18/4/2017 20:06	65	20/4/2017 21:11	65	22/4/2017 22:16	66	23/4/2017 15:21	66	24/4/2017 20:26	66	26/4/2017 21:31	65
18/4/2017 20:11	65	20/4/2017 21:16	65	22/4/2017 22:21	66	23/4/2017 15:26	57	24/4/2017 20:31	66	26/4/2017 21:36	66
18/4/2017 20:16	65	20/4/2017 21:21	65	22/4/2017 22:26	66	23/4/2017 15:31	57	24/4/2017 20:36	65	26/4/2017 21:41	57
18/4/2017 20:21	66	20/4/2017 21:26	65	22/4/2017 22:31	66	23/4/2017 15:36	66	24/4/2017 20:41	66	26/4/2017 21:46	66
18/4/2017 20:26	65	20/4/2017 21:31	65	22/4/2017 22:36	66	23/4/2017 15:41	66	24/4/2017 20:46	66	26/4/2017 21:51	66
18/4/2017 20:31	66	20/4/2017 21:36	65	22/4/2017 22:41	65	23/4/2017 15:46	66	24/4/2017 20:51	66	26/4/2017 21:56	66
18/4/2017 20:36	65	20/4/2017 21:41	65	22/4/2017 22:46	49	23/4/2017 15:51	66	24/4/2017 20:56	65	26/4/2017 22:01	66
18/4/2017 20:41	65	20/4/2017 21:46	65	22/4/2017 22:51	66	23/4/2017 15:56	66	24/4/2017 21:01	65	26/4/2017 22:06	66
18/4/2017 20:46	65	20/4/2017 21:51	65	22/4/2017 22:56	65	23/4/2017 16:01	66	24/4/2017 21:06	66	26/4/2017 22:11	58
18/4/2017 20:51	64	20/4/2017 21:56	65	23/4/2017 7:01	64	23/4/2017 16:06	65	24/4/2017 21:11	65	26/4/2017 22:16	66
18/4/2017 20:56	65	20/4/2017 22:01	65	23/4/2017 7:06	64	23/4/2017 16:11	65	24/4/2017 21:16	65	26/4/2017 22:21	66
18/4/2017 21:01	65	20/4/2017 22:06	65	23/4/2017 7:11	65	23/4/2017 16:16	66	24/4/2017 21:21	66	26/4/2017 22:26	65
18/4/2017 21:06	65	20/4/2017 22:11	66	23/4/2017 7:16	66	23/4/2017 16:21	43	24/4/2017 21:26	66	26/4/2017 22:31	66
18/4/2017 21:11	65	20/4/2017 22:16	65	23/4/2017 7:21	64	23/4/2017 16:26	66	24/4/2017 21:31	65	26/4/2017 22:36	66
18/4/2017 21:16	65	20/4/2017 22:21	65	23/4/2017 7:26	66	23/4/2017 16:31	45	24/4/2017 21:36	65	26/4/2017 22:41	66
18/4/2017 21:21	65	20/4/2017 22:26	66	23/4/2017 7:31	64	23/4/2017 16:36	47	24/4/2017 21:41	66	26/4/2017 22:46	66
18/4/2017 21:26	65	20/4/2017 22:31	66	23/4/2017 7:36	64	23/4/2017 16:41	66	24/4/2017 21:46	65	26/4/2017 22:51	65
18/4/2017 21:31	65	20/4/2017 22:36	65	23/4/2017 7:41	64	23/4/2017 16:46	66	24/4/2017 21:51	65	26/4/2017 22:56	65
18/4/2017 21:36	65	20/4/2017 22:41	66	23/4/2017 7:46	66	23/4/2017 16:51	50	24/4/2017 21:56	66		
18/4/2017 21:41	65	20/4/2017 22:46	65	23/4/2017 7:51	64	23/4/2017 16:56	66	24/4/2017 22:01	65	Night time: 23:00-07:00	
18/4/2017 21:46	64	20/4/2017 22:51	65	23/4/2017 7:56	66	23/4/2017 17:01	66	24/4/2017 22:06	65		
18/4/2017 21:51	65	20/4/2017 22:56	64	23/4/2017 8:01	64	23/4/2017 17:06	66	24/4/2017 22:11	65	27/2/2017 0:01	49
18/4/2017 21:56	65	21/4/2017 19:01	64	23/4/2017 8:06	65	23/4/2017 17:11	66	24/4/2017 22:16	65	27/3/2017 0:01	54
18/4/2017 22:01	65	21/4/2017 19:06	63	23/4/2017 8:11	65	23/4/2017 17:16	66	24/4/2017 22:21	65	27/3/2017 0:06	63
18/4/2017 22:06	65	21/4/2017 19:11	63	23/4/2017 8:16	65	23/4/2017 17:21	66	24/4/2017 22:26	65	27/3/2017 0:11	63
18/4/2017 22:11	64	21/4/2017 19:16	62	23/4/2017 8:21	65	23/4/2017 17:26	53	24/4/2017 22:31	65	27/3/2017 0:16	48
18/4/2017 22:16	64	21/4/2017 19:21	63	23/4/2017 8:26	66	23/4/2017 17:31	66	24/4/2017 22:36	66	27/3/2017 0:21	62
18/4/2017 22:21	64	21/4/2017 19:26	63	23/4/2017 8:31	65	23/4/2017 17:36	52	24/4/2017 22:41	66	27/3/2017 0:26	62
18/4/2017 22:26	65	21/4/2017 19:31	66	23/4/2017 8:36	50	23/4/2017 17:41	56	24/4/2017 22:46	65	27/3/2017 0:31	46
18/4/2017 22:31	64	21/4/2017 19:36	65	23/4/2017 8:41	55	23/4/2017 17:46	55	24/4/2017 22:51	65	27/3/2017 0:36	49
18/4/2017 22:36	64	21/4/2017 19:41	65	23/4/2017 8:46	65	23/4/2017 17:51	66	24/4/2017 22:56	66	27/3/2017 0:41	63
18/4/2017 22:41	65	21/4/2017 19:46	66	23/4/2017 8:51	65	23/4/2017 17:56	66	25/4/2017 19:01	65	27/3/2017 0:46	62
18/4/2017 22:46	64	21/4/2017 19:51	66	23/4/2017 8:56	49	23/4/2017 18:01	66	25/4/2017 19:06	64	27/3/2017 0:51	62
18/4/2017 22:51	65	21/4/2017 19:56	65	23/4/2017 9:01	66	23/4/2017 18:06	66	25/4/2017 19:11	64	27/3/2017 0:56	61
18/4/2017 22:56	65	21/4/2017 20:01	66	23/4/2017 9:06	66	23/4/2017 18:11	66	25/4/2017 19:16	66	27/3/2017 1:01	62
19/4/2017 19:01	66	21/4/2017 20:06	65	23/4/2017 9:11	66	23/4/2017 18:16	66	25/4/2017 19:21	66	27/3/2017 1:06	62
19/4/2017 19:06	66	21/4/2017 20:11	66	23/4/2017 9:16	65	23/4/2017 18:21	51	25/4/2017 19:26	66	27/3/2017 1:11	62
19/4/2017 19:11	66	21/4/2017 20:16	65	23/4/2017 9:21	66	23/4/2017 18:26	53	25/4/2017 19:31	66	27/3/2017 1:16	61
19/4/2017 19:16	65	21/4/2017 20:21	66	23/4/2017 9:26	66	23/4/2017 18:31	66	25/4/2017 19:36	66	27/3/2017 1:21	62
19/4/2017 19:21	65	21/4/2017 20:26	65	23/4/2017 9:31	66	23/4/2017 18:36	58	25/4/2017 19:41	66	27/3/2017 1:26	61
19/4/2017 19:26	66	21/4/2017 20:31	66	23/4/2017 9:36	66	23/4/2017 18:41	66	25/4/2017 19:46	66	27/3/2017 1:31	60
19/4/2017 19:31	66	21/4/2017 20:36	66	23/4/2017 9:41	46	23/4/2017 18:46	66	25/4/2017 19:51	66	27/3/2017 1:36	61
19/4/2017 19:36	65	21/4/2017 20:41	66	23/4/2017 9:46	66	23/4/2017 18:51	66	25/4/2017 19:56	66	27/3/2017 1:41	60
19/4/2017 19:41	66	21/4/2017 20:46	65	23/4/2017 9:51	66	23/4/2017 18:56	66	25/4/2017 20:01	66	27/3/2017 1:46	59
19/4/2017 19:46	49	21/4/2017 20:51	65	23/4/2017 9:56	66	23/4/2017 19:01	66	25/4/2017 20:06	66	27/3/2017 1:51	60
19/4/2017 19:51	66	21/4/2017 20:56	65	23/4/2017 10:01	66	23/4/2017 19:06	66	25/4/2017 20:11	66	27/3/2017 1:56	59
19/4/2017 19:56	65	21/4/2017 21:01	65	23/4/2017 10:06	66	23/4/2017 19:11	51	25/4/2017 20:16	46	27/3/2017 2:01	59
19/4/2017 20:01	65	21/4/2017 21:06	65	23/4/2017 10:11	66	23/4/2017 19:16	65	25/4/2017 20:21	66	27/3/2017 2:06	58
19/4/2017 20:06	65	21/4/2017 21:11	65	23/4/2017 10:16	66	23/4/2017 19:21	66	25/4/2017 20:26	66	27/3/2017 2:11	60
19/4/2017 20:11	65	21/4/2017 21:16	65	23/4/2017 10:21	66	23/4/2017 19:26	65	25/4/2017 20:31	66	27/3/2017 2:16	60
19/4/2017 20:16	66	21/4/2017 21:21	66	23/4/2017 10:26	58	23/4/2017 19:31	66	25/4/2017 20:36	66	27/3/2017 2:21	59
19/4/2017 20:21	65	21/4/2017 21:26	65	23/4/2017 10:31	66	23/4/2017 19:36	66	25/4/2017 20:41	66	27/3/2017 2:26	59
19/4/2017 20:26	65	21/4/2017 21:31	65	23/4/2017 10:36	52	23/4/2017 19:41	66	25/4/2017 20:46	66	27/3/2017 2:31	60
19/4/2017 20:31	65	21/4/2017 21:36	65	23/4/2017 10:41	66	23/4/2017 19:46	66	25/4/2017 20:51	66	27/3/2017 2:36	59
19/4/2017 20:36	65	21/4/2017 21:41	65	23/4/2017 10:46	66	23/4/2017 19:51	66	25/4/2017 20:5			

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
27/3/2017 5:41	60	28/3/2017 6:46	63	29/3/2017 23:51	57	31/3/2017 0:56	48	1/4/2017 2:01	54	2/4/2017 3:06	62
27/3/2017 5:46	62	28/3/2017 6:51	64	29/3/2017 23:56	59	31/3/2017 1:01	63	1/4/2017 2:06	56	2/4/2017 3:11	62
27/3/2017 5:51	62	28/3/2017 6:56	64	30/3/2017 0:01	58	31/3/2017 1:06	63	1/4/2017 2:11	56	2/4/2017 3:16	63
27/3/2017 5:56	62	28/3/2017 23:01	60	30/3/2017 0:06	58	31/3/2017 1:11	63	1/4/2017 2:16	63	2/4/2017 3:21	62
27/3/2017 6:01	62	28/3/2017 23:06	62	30/3/2017 0:11	53	31/3/2017 1:16	62	1/4/2017 2:21	55	2/4/2017 3:26	62
27/3/2017 6:06	62	28/3/2017 23:11	58	30/3/2017 0:16	53	31/3/2017 1:21	62	1/4/2017 2:26	57	2/4/2017 3:31	61
27/3/2017 6:11	55	28/3/2017 23:16	59	30/3/2017 0:21	58	31/3/2017 1:26	61	1/4/2017 2:31	63	2/4/2017 3:36	63
27/3/2017 6:16	63	28/3/2017 23:21	57	30/3/2017 0:26	55	31/3/2017 1:31	62	1/4/2017 2:36	59	2/4/2017 3:41	61
27/3/2017 6:21	59	28/3/2017 23:26	57	30/3/2017 0:31	62	31/3/2017 1:36	62	1/4/2017 2:41	63	2/4/2017 3:46	61
27/3/2017 6:26	59	28/3/2017 23:31	59	30/3/2017 0:36	63	31/3/2017 1:41	61	1/4/2017 2:46	63	2/4/2017 3:51	62
27/3/2017 6:31	60	28/3/2017 23:36	58	30/3/2017 0:41	57	31/3/2017 1:46	61	1/4/2017 2:51	58	2/4/2017 3:56	62
27/3/2017 6:36	61	28/3/2017 23:41	56	30/3/2017 0:46	63	31/3/2017 1:51	62	1/4/2017 2:56	48	2/4/2017 4:01	61
27/3/2017 6:41	62	28/3/2017 23:46	56	30/3/2017 0:51	62	31/3/2017 1:56	62	1/4/2017 3:01	55	2/4/2017 4:06	61
27/3/2017 6:46	63	28/3/2017 23:51	56	30/3/2017 0:56	62	31/3/2017 2:01	62	1/4/2017 3:06	63	2/4/2017 4:11	61
27/3/2017 6:51	64	28/3/2017 23:56	51	30/3/2017 1:01	54	31/3/2017 2:06	60	1/4/2017 3:11	63	2/4/2017 4:16	61
27/3/2017 6:56	64	29/3/2017 0:01	63	30/3/2017 1:06	61	31/3/2017 2:11	61	1/4/2017 3:16	63	2/4/2017 4:21	61
27/3/2017 23:01	63	29/3/2017 0:06	54	30/3/2017 1:11	40	31/3/2017 2:16	61	1/4/2017 3:21	62	2/4/2017 4:26	60
27/3/2017 23:06	58	29/3/2017 0:11	63	30/3/2017 1:16	63	31/3/2017 2:21	62	1/4/2017 3:26	62	2/4/2017 4:31	61
27/3/2017 23:11	60	29/3/2017 0:16	54	30/3/2017 1:21	63	31/3/2017 2:26	61	1/4/2017 3:31	46	2/4/2017 4:36	61
27/3/2017 23:16	56	29/3/2017 0:21	63	30/3/2017 1:26	62	31/3/2017 2:31	61	1/4/2017 3:36	63	2/4/2017 4:41	61
27/3/2017 23:21	57	29/3/2017 0:26	48	30/3/2017 1:31	62	31/3/2017 2:36	60	1/4/2017 3:41	61	2/4/2017 4:46	60
27/3/2017 23:26	57	29/3/2017 0:31	58	30/3/2017 1:36	61	31/3/2017 2:41	60	1/4/2017 3:46	62	2/4/2017 4:51	61
27/3/2017 23:31	57	29/3/2017 0:36	55	30/3/2017 1:41	62	31/3/2017 2:46	59	1/4/2017 3:51	63	2/4/2017 4:56	60
27/3/2017 23:36	50	29/3/2017 0:41	51	30/3/2017 1:46	61	31/3/2017 2:51	60	1/4/2017 3:56	61	2/4/2017 5:01	61
27/3/2017 23:41	54	29/3/2017 0:46	54	30/3/2017 1:51	63	31/3/2017 2:56	61	1/4/2017 4:01	61	2/4/2017 5:06	60
27/3/2017 23:46	50	29/3/2017 0:51	62	30/3/2017 1:56	61	31/3/2017 3:01	60	1/4/2017 4:06	62	2/4/2017 5:11	61
27/3/2017 23:51	40	29/3/2017 0:56	63	30/3/2017 2:01	62	31/3/2017 3:06	60	1/4/2017 4:11	62	2/4/2017 5:16	60
27/3/2017 23:56	56	29/3/2017 1:01	63	30/3/2017 2:06	61	31/3/2017 3:11	60	1/4/2017 4:16	61	2/4/2017 5:21	60
28/3/2017 0:01	55	29/3/2017 1:06	63	30/3/2017 2:11	60	31/3/2017 3:16	59	1/4/2017 4:21	62	2/4/2017 5:26	61
28/3/2017 0:06	63	29/3/2017 1:11	63	30/3/2017 2:16	61	31/3/2017 3:21	60	1/4/2017 4:26	63	2/4/2017 5:31	62
28/3/2017 0:11	54	29/3/2017 1:16	63	30/3/2017 2:21	60	31/3/2017 3:26	60	1/4/2017 4:31	63	2/4/2017 5:36	61
28/3/2017 0:16	53	29/3/2017 1:21	62	30/3/2017 2:26	60	31/3/2017 3:31	60	1/4/2017 4:36	62	2/4/2017 5:41	61
28/3/2017 0:21	57	29/3/2017 1:26	61	30/3/2017 2:31	60	31/3/2017 3:36	60	1/4/2017 4:41	61	2/4/2017 5:46	61
28/3/2017 0:26	63	29/3/2017 1:31	63	30/3/2017 2:36	62	31/3/2017 3:41	59	1/4/2017 4:46	63	2/4/2017 5:51	55
28/3/2017 0:31	63	29/3/2017 1:36	62	30/3/2017 2:41	61	31/3/2017 3:46	59	1/4/2017 4:51	61	2/4/2017 5:56	63
28/3/2017 0:36	62	29/3/2017 1:41	61	30/3/2017 2:46	61	31/3/2017 3:51	60	1/4/2017 4:56	61	2/4/2017 6:01	62
28/3/2017 0:41	62	29/3/2017 1:46	62	30/3/2017 2:51	61	31/3/2017 3:56	59	1/4/2017 5:01	63	2/4/2017 6:06	62
28/3/2017 0:46	49	29/3/2017 1:51	61	30/3/2017 2:56	60	31/3/2017 4:01	59	1/4/2017 5:06	62	2/4/2017 6:11	62
28/3/2017 0:51	61	29/3/2017 1:56	60	30/3/2017 3:01	60	31/3/2017 4:06	58	1/4/2017 5:11	63	2/4/2017 6:16	56
28/3/2017 0:56	62	29/3/2017 2:01	60	30/3/2017 3:06	60	31/3/2017 4:11	60	1/4/2017 5:16	62	2/4/2017 6:21	48
28/3/2017 1:01	63	29/3/2017 2:06	61	30/3/2017 3:11	59	31/3/2017 4:16	59	1/4/2017 5:21	63	2/4/2017 6:26	58
28/3/2017 1:06	62	29/3/2017 2:11	61	30/3/2017 3:16	59	31/3/2017 4:21	60	1/4/2017 5:26	63	2/4/2017 6:31	57
28/3/2017 1:11	63	29/3/2017 2:16	61	30/3/2017 3:21	60	31/3/2017 4:26	60	1/4/2017 5:31	54	2/4/2017 6:36	59
28/3/2017 1:16	63	29/3/2017 2:21	62	30/3/2017 3:26	59	31/3/2017 4:31	59	1/4/2017 5:36	45	2/4/2017 6:41	60
28/3/2017 1:21	62	29/3/2017 2:26	61	30/3/2017 3:31	61	31/3/2017 4:36	59	1/4/2017 5:41	63	2/4/2017 6:46	59
28/3/2017 1:26	61	29/3/2017 2:31	61	30/3/2017 3:36	61	31/3/2017 4:41	60	1/4/2017 5:46	63	2/4/2017 6:51	58
28/3/2017 1:31	61	29/3/2017 2:36	60	30/3/2017 3:41	60	31/3/2017 4:46	59	1/4/2017 5:51	63	2/4/2017 6:56	60
28/3/2017 1:36	62	29/3/2017 2:41	60	30/3/2017 3:46	60	31/3/2017 4:51	59	1/4/2017 5:56	63	2/4/2017 23:01	57
28/3/2017 1:41	62	29/3/2017 2:46	60	30/3/2017 3:51	59	31/3/2017 4:56	61	1/4/2017 6:01	55	2/4/2017 23:06	55
28/3/2017 1:46	61	29/3/2017 2:51	60	30/3/2017 3:56	59	31/3/2017 5:01	59	1/4/2017 6:06	63	2/4/2017 23:11	57
28/3/2017 1:51	61	29/3/2017 2:56	60	30/3/2017 4:01	58	31/3/2017 5:06	59	1/4/2017 6:11	58	2/4/2017 23:16	57
28/3/2017 1:56	61	29/3/2017 3:01	60	30/3/2017 4:06	59	31/3/2017 5:11	59	1/4/2017 6:16	57	2/4/2017 23:21	56
28/3/2017 2:01	61	29/3/2017 3:06	59	30/3/2017 4:11	60	31/3/2017 5:16	60	1/4/2017 6:21	60	2/4/2017 23:26	57
28/3/2017 2:06	61	29/3/2017 3:11	59	30/3/2017 4:16	59	31/3/2017 5:21	61	1/4/2017 6:26	61	2/4/2017 23:31	55
28/3/2017 2:11	61	29/3/2017 3:16	58	30/3/2017 4:21	61	31/3/2017 5:26	61	1/4/2017 6:31	55	2/4/2017 23:36	63
28/3/2017 2:16	60	29/3/2017 3:21	59	30/3/2017 4:26	60	31/3/2017 5:31	61	1/4/2017 6:36	61	2/4/2017 23:41	54
28/3/2017 2:21	60	29/3/2017 3:26	58	30/3/2017 4:31	60	31/3/2017 5:36	62	1/4/2017 6:41	62	2/4/2017 23:46	56
28/3/2017 2:26	60	29/3/2017 3:31	59	30/3/2017 4:36	58	31/3/2017 5:41	60	1/4/2017 6:46	61	2/4/2017 23:51	62
28/3/2017 2:31	59	29/3/2017 3:36	61	30/3/2017 4:41	60	31/3/2017 5:46	61	1/4/2017 6:51	63	2/4/2017 23:56	48
28/3/2017 2:36	60	29/3/2017 3:41	59	30/3/2017 4:46	59	31/3/2017 5:51	61	1/4/2017 6:56	63	3/4/2017 0:01	63
28/3/2017 2:41	60	29/3/2017 3:46	60	30/3/2017 4:51	60	31/3/2017 5:56	62	1/4/2017 23:01	59	3/4/2017 0:06	54
28/3/2017 2:46	59	29/3/2017 3:51	59	30/3/2017 4:56	60	31/3/2017 6:01	62	1/4/2017 23:06	59	3/4/2017 0:11	63
28/3/2017 2:51	63	29/3/2017 3:56	60	30/3/2017 5:01	59	31/3/2017 6:06	63	1/4/2017 23:11	60	3/4/2017 0:16	46
28/3/2017 2:56	59	29/3/2017 4:01	59	30/3/2017 5:06	58	31/3/2017 6:11	51	1/4/2017 23:16	57	3/4/2017 0:21	62
28/3/2017 3:01	59	29/3/2017 4:06	60	30/3/2017 5:11	59	31/3/2017 6:16	52	1/4/2017 23:21	59	3/4/2017 0:26	63
28/3/2017 3:06	59	29/3/2017 4:11	60	30/3/2017 5:16	60	31/3/2017 6:21	61	1/4/2017 23:26	59	3/4/2017 0:31	63
28/3/2017 3:11	60	29/3/2017 4:16	60	30/3/2017 5:21	60	31/3/2017 6:26	63	1/4/2017 23:31	59	3/4/2017 0:36	62
28/3/2017 3:16	60	29/3/2017 4:21	58	30/3/2017 5:26	62	31/3/2017 6:31	61	1/4/2017 23:36	59	3/4/2017 0:41	62
28/3/2017 3:21	59	29/3/2017 4:26	60	30/3/2017 5:31	61	31/3/2017 6:36	60	1/4/2017 23:41	59	3/4/2017 0:46	63
28/3/2017 3:26	63	29/3/2017 4:31	60	30/3/2017 5:36	61	31/3/2017 6:41	60	1/4/2017 23:46	60	3/4/2017 0:51	61
28/3/2017 3:31	60	29/3/2017 4:36	60	30/3/2017 5:41	61	31/3/2017 6:46	61	1/4/2017 23:51	58	3/4/2017 0:56	62
28/3/2017 3:36	59	29/3/2017 4:41	59	30/3/2017 5:46	62	31/3/2017 6:51	64	1/4/2017 23:56	58	3/4/2017 1:01	61
28/3/2017 3:41	59	29/3/2017 4:46	59	30/3/2017 5:51	63	31/3/2017 6:56	63	2/4/2017 0:01	58	3/4/2017 1:06	62
28/3/2017 3:46	60	29/3/2017 4:51	59	30/3/2017 5:56	62	31/3/2017 23:01	63	2/4/2017 0:06	58	3/4/2017 1:11	62
28/3/2017 3:51	59	29/3/2017 4:56	60	30/3/2017 6:01	61	31/3/2017 23:06	61	2/4/2017 0:11	56	3/4/2017 1:16	61
28/3/2017 3:56	60	29/3/2017 5:01	59	30/3/2017 6:06	63	31/3/2017 23:11	64	2/4/2017 0:16	57	3/4/2017 1:21	61
28/3/2017 4:01	58	29/3/2017 5:06	59	30/3/2017 6:11	63	31					

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
3/4/2017 4:11	58	4/4/2017 5:16	59	5/4/2017 6:21	57	6/4/2017 23:26	55	8/4/2017 0:31	59	9/4/2017 1:36	62
3/4/2017 4:16	60	4/4/2017 5:21	60	5/4/2017 6:26	60	6/4/2017 23:31	58	8/4/2017 0:36	57	9/4/2017 1:41	62
3/4/2017 4:21	58	4/4/2017 5:26	61	5/4/2017 6:31	62	6/4/2017 23:36	57	8/4/2017 0:41	53	9/4/2017 1:46	62
3/4/2017 4:26	60	4/4/2017 5:31	61	5/4/2017 6:36	61	6/4/2017 23:41	58	8/4/2017 0:46	55	9/4/2017 1:51	63
3/4/2017 4:31	59	4/4/2017 5:36	61	5/4/2017 6:41	62	6/4/2017 23:46	52	8/4/2017 0:51	48	9/4/2017 1:56	62
3/4/2017 4:36	60	4/4/2017 5:41	61	5/4/2017 6:46	62	6/4/2017 23:51	57	8/4/2017 0:56	54	9/4/2017 2:01	62
3/4/2017 4:41	59	4/4/2017 5:46	60	5/4/2017 6:51	62	6/4/2017 23:56	57	8/4/2017 1:01	58	9/4/2017 2:06	62
3/4/2017 4:46	59	4/4/2017 5:51	62	5/4/2017 6:56	63	7/4/2017 0:01	53	8/4/2017 1:06	40	9/4/2017 2:11	61
3/4/2017 4:51	59	4/4/2017 5:56	62	5/4/2017 23:01	58	7/4/2017 0:06	47	8/4/2017 1:11	56	9/4/2017 2:16	62
3/4/2017 4:56	61	4/4/2017 6:01	63	5/4/2017 23:06	59	7/4/2017 0:11	56	8/4/2017 1:16	55	9/4/2017 2:21	62
3/4/2017 5:01	59	4/4/2017 6:06	62	5/4/2017 23:11	59	7/4/2017 0:16	54	8/4/2017 1:21	56	9/4/2017 2:26	62
3/4/2017 5:06	61	4/4/2017 6:11	63	5/4/2017 23:16	58	7/4/2017 0:21	57	8/4/2017 1:26	63	9/4/2017 2:31	43
3/4/2017 5:11	60	4/4/2017 6:16	63	5/4/2017 23:21	58	7/4/2017 0:26	48	8/4/2017 1:31	63	9/4/2017 2:36	61
3/4/2017 5:16	59	4/4/2017 6:21	48	5/4/2017 23:26	58	7/4/2017 0:31	63	8/4/2017 1:36	63	9/4/2017 2:41	62
3/4/2017 5:21	60	4/4/2017 6:26	63	5/4/2017 23:31	59	7/4/2017 0:36	53	8/4/2017 1:41	50	9/4/2017 2:46	61
3/4/2017 5:26	61	4/4/2017 6:31	55	5/4/2017 23:36	59	7/4/2017 0:41	63	8/4/2017 1:46	47	9/4/2017 2:51	60
3/4/2017 5:31	61	4/4/2017 6:36	58	5/4/2017 23:41	57	7/4/2017 0:46	48	8/4/2017 1:51	63	9/4/2017 2:56	62
3/4/2017 5:36	61	4/4/2017 6:41	63	5/4/2017 23:46	57	7/4/2017 0:51	63	8/4/2017 1:56	63	9/4/2017 3:01	61
3/4/2017 5:41	62	4/4/2017 6:46	58	5/4/2017 23:51	57	7/4/2017 0:56	62	8/4/2017 2:01	63	9/4/2017 3:06	61
3/4/2017 5:46	62	4/4/2017 6:51	56	5/4/2017 23:56	53	7/4/2017 1:01	62	8/4/2017 2:06	62	9/4/2017 3:11	61
3/4/2017 5:51	61	4/4/2017 6:56	59	6/4/2017 0:01	54	7/4/2017 1:06	63	8/4/2017 2:11	62	9/4/2017 3:16	61
3/4/2017 5:56	63	4/4/2017 23:01	57	6/4/2017 0:06	52	7/4/2017 1:11	61	8/4/2017 2:16	62	9/4/2017 3:21	61
3/4/2017 6:01	62	4/4/2017 23:06	52	6/4/2017 0:11	56	7/4/2017 1:16	61	8/4/2017 2:21	52	9/4/2017 3:26	62
3/4/2017 6:06	62	4/4/2017 23:11	49	6/4/2017 0:16	53	7/4/2017 1:21	62	8/4/2017 2:26	62	9/4/2017 3:31	61
3/4/2017 6:11	51	4/4/2017 23:16	56	6/4/2017 0:21	58	7/4/2017 1:26	62	8/4/2017 2:31	63	9/4/2017 3:36	62
3/4/2017 6:16	58	4/4/2017 23:21	57	6/4/2017 0:26	56	7/4/2017 1:31	61	8/4/2017 2:36	63	9/4/2017 3:41	61
3/4/2017 6:21	59	4/4/2017 23:26	63	6/4/2017 0:31	55	7/4/2017 1:36	61	8/4/2017 2:41	62	9/4/2017 3:46	61
3/4/2017 6:26	59	4/4/2017 23:31	50	6/4/2017 0:36	51	7/4/2017 1:41	61	8/4/2017 2:46	62	9/4/2017 3:51	61
3/4/2017 6:31	58	4/4/2017 23:36	49	6/4/2017 0:41	63	7/4/2017 1:46	61	8/4/2017 2:51	62	9/4/2017 3:56	61
3/4/2017 6:36	61	4/4/2017 23:41	44	6/4/2017 0:46	48	7/4/2017 1:51	61	8/4/2017 2:56	61	9/4/2017 4:01	60
3/4/2017 6:41	62	4/4/2017 23:46	63	6/4/2017 0:51	62	7/4/2017 1:56	61	8/4/2017 3:01	62	9/4/2017 4:06	60
3/4/2017 6:46	64	4/4/2017 23:51	63	6/4/2017 0:56	62	7/4/2017 2:01	61	8/4/2017 3:06	62	9/4/2017 4:11	61
3/4/2017 6:51	63	4/4/2017 23:56	60	6/4/2017 1:01	62	7/4/2017 2:06	62	8/4/2017 3:11	62	9/4/2017 4:16	61
3/4/2017 6:56	63	5/4/2017 0:01	62	6/4/2017 1:06	61	7/4/2017 2:11	61	8/4/2017 3:16	62	9/4/2017 4:21	61
3/4/2017 23:01	58	5/4/2017 0:06	45	6/4/2017 1:11	63	7/4/2017 2:16	61	8/4/2017 3:21	62	9/4/2017 4:26	61
3/4/2017 23:06	58	5/4/2017 0:11	63	6/4/2017 1:16	62	7/4/2017 2:21	60	8/4/2017 3:26	61	9/4/2017 4:31	61
3/4/2017 23:11	63	5/4/2017 0:16	63	6/4/2017 1:21	61	7/4/2017 2:26	60	8/4/2017 3:31	61	9/4/2017 4:36	61
3/4/2017 23:16	60	5/4/2017 0:21	62	6/4/2017 1:26	62	7/4/2017 2:31	60	8/4/2017 3:36	61	9/4/2017 4:41	60
3/4/2017 23:21	60	5/4/2017 0:26	48	6/4/2017 1:31	61	7/4/2017 2:36	61	8/4/2017 3:41	61	9/4/2017 4:46	61
3/4/2017 23:26	58	5/4/2017 0:31	63	6/4/2017 1:36	61	7/4/2017 2:41	60	8/4/2017 3:46	62	9/4/2017 4:51	60
3/4/2017 23:31	57	5/4/2017 0:36	63	6/4/2017 1:41	61	7/4/2017 2:46	61	8/4/2017 3:51	61	9/4/2017 4:56	60
3/4/2017 23:36	57	5/4/2017 0:41	61	6/4/2017 1:46	61	7/4/2017 2:51	60	8/4/2017 3:56	63	9/4/2017 5:01	60
3/4/2017 23:41	58	5/4/2017 0:46	61	6/4/2017 1:51	63	7/4/2017 2:56	60	8/4/2017 4:01	60	9/4/2017 5:06	60
3/4/2017 23:46	59	5/4/2017 0:51	62	6/4/2017 1:56	61	7/4/2017 3:01	60	8/4/2017 4:06	60	9/4/2017 5:11	61
3/4/2017 23:51	61	5/4/2017 0:56	61	6/4/2017 2:01	61	7/4/2017 3:06	61	8/4/2017 4:11	61	9/4/2017 5:16	59
3/4/2017 23:56	59	5/4/2017 1:01	62	6/4/2017 2:06	60	7/4/2017 3:11	59	8/4/2017 4:16	62	9/4/2017 5:21	60
4/4/2017 0:01	60	5/4/2017 1:06	61	6/4/2017 2:11	60	7/4/2017 3:16	62	8/4/2017 4:21	61	9/4/2017 5:26	62
4/4/2017 0:06	51	5/4/2017 1:11	62	6/4/2017 2:16	61	7/4/2017 3:21	61	8/4/2017 4:26	62	9/4/2017 5:31	61
4/4/2017 0:11	54	5/4/2017 1:16	60	6/4/2017 2:21	60	7/4/2017 3:26	59	8/4/2017 4:31	61	9/4/2017 5:36	62
4/4/2017 0:16	53	5/4/2017 1:21	62	6/4/2017 2:26	60	7/4/2017 3:31	60	8/4/2017 4:36	61	9/4/2017 5:41	62
4/4/2017 0:21	60	5/4/2017 1:26	61	6/4/2017 2:31	60	7/4/2017 3:36	59	8/4/2017 4:41	62	9/4/2017 5:46	62
4/4/2017 0:26	60	5/4/2017 1:31	60	6/4/2017 2:36	60	7/4/2017 3:41	58	8/4/2017 4:46	60	9/4/2017 5:51	61
4/4/2017 0:31	54	5/4/2017 1:36	62	6/4/2017 2:41	60	7/4/2017 3:46	59	8/4/2017 4:51	61	9/4/2017 5:56	62
4/4/2017 0:36	46	5/4/2017 1:41	59	6/4/2017 2:46	59	7/4/2017 3:51	60	8/4/2017 4:56	62	9/4/2017 6:01	63
4/4/2017 0:41	55	5/4/2017 1:46	60	6/4/2017 2:51	60	7/4/2017 3:56	60	8/4/2017 5:01	61	9/4/2017 6:06	62
4/4/2017 0:46	54	5/4/2017 1:51	61	6/4/2017 2:56	61	7/4/2017 4:01	59	8/4/2017 5:06	61	9/4/2017 6:11	55
4/4/2017 0:51	53	5/4/2017 1:56	59	6/4/2017 3:01	60	7/4/2017 4:06	61	8/4/2017 5:11	61	9/4/2017 6:16	51
4/4/2017 0:56	63	5/4/2017 2:01	60	6/4/2017 3:06	59	7/4/2017 4:11	60	8/4/2017 5:16	60	9/4/2017 6:21	63
4/4/2017 1:01	63	5/4/2017 2:06	61	6/4/2017 3:11	58	7/4/2017 4:16	58	8/4/2017 5:21	61	9/4/2017 6:26	54
4/4/2017 1:06	55	5/4/2017 2:11	59	6/4/2017 3:16	59	7/4/2017 4:21	60	8/4/2017 5:26	61	9/4/2017 6:31	64
4/4/2017 1:11	63	5/4/2017 2:16	60	6/4/2017 3:21	58	7/4/2017 4:26	59	8/4/2017 5:31	60	9/4/2017 6:36	57
4/4/2017 1:16	63	5/4/2017 2:21	62	6/4/2017 3:26	58	7/4/2017 4:31	61	8/4/2017 5:36	62	9/4/2017 6:41	55
4/4/2017 1:21	63	5/4/2017 2:26	59	6/4/2017 3:31	60	7/4/2017 4:36	59	8/4/2017 5:41	61	9/4/2017 6:46	57
4/4/2017 1:26	48	5/4/2017 2:31	58	6/4/2017 3:36	60	7/4/2017 4:41	58	8/4/2017 5:46	62	9/4/2017 6:51	68
4/4/2017 1:31	63	5/4/2017 2:36	62	6/4/2017 3:41	59	7/4/2017 4:46	60	8/4/2017 5:51	62	9/4/2017 6:56	56
4/4/2017 1:36	63	5/4/2017 2:41	59	6/4/2017 3:46	58	7/4/2017 4:51	60	8/4/2017 5:56	62	9/4/2017 23:01	58
4/4/2017 1:41	63	5/4/2017 2:46	60	6/4/2017 3:51	57	7/4/2017 4:56	60	8/4/2017 6:01	62	9/4/2017 23:06	53
4/4/2017 1:46	56	5/4/2017 2:51	59	6/4/2017 3:56	58	7/4/2017 5:01	60	8/4/2017 6:06	62	9/4/2017 23:11	54
4/4/2017 1:51	62	5/4/2017 2:56	59	6/4/2017 4:01	57	7/4/2017 5:06	59	8/4/2017 6:11	56	9/4/2017 23:16	55
4/4/2017 1:56	62	5/4/2017 3:01	58	6/4/2017 4:06	59	7/4/2017 5:11	60	8/4/2017 6:16	57	9/4/2017 23:21	55
4/4/2017 2:01	62	5/4/2017 3:06	59	6/4/2017 4:11	58	7/4/2017 5:16	59	8/4/2017 6:21	53	9/4/2017 23:26	63
4/4/2017 2:06	62	5/4/2017 3:11	61	6/4/2017 4:16	59	7/4/2017 5:21	61	8/4/2017 6:26	59	9/4/2017 23:31	53
4/4/2017 2:11	63	5/4/2017 3:16	58	6/4/2017 4:21	58	7/4/2017 5:26	61	8/4/2017 6:31	59	9/4/2017 23:36	45
4/4/2017 2:16	62	5/4/2017 3:21	59	6/4/2017 4:26	58	7/4/2017 5:31	62	8/4/2017 6:36	58	9/4/2017 23:41	49
4/4/2017 2:21	62	5/4/2017 3:26	61	6/4/2017 4:31	59	7/4/2017 5:36	61	8/4/2017 6:41	62	9/4/2017 23:46	52
4/4/2017 2:26	61	5/4/2017 3:31	59	6/4/2017 4:36	60	7/4/2017 5:41	62	8/4/2017 6:46	60	9/4/2017 23:51	63
4/4/2017 2:31	63	5/4/2017 3:36	59	6/4/2017 4:41	59	7/4/2017 5:46	62	8/4/2017 6:51	60	9/4/2017 23:56	37
4/4/2017 2:36	62	5/4/2017 3:41	58	6/4/2017 4:46	59	7/4/2017 5:51	62	8/4/2017 6:56	61	10/4/2017 0:01	62
4/4/2017 2:41	62	5/4/2017 3:46	57	6/4/2017 4:51	58</						

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
10/4/2017 2:41	57	11/4/2017 3:46	59	12/4/2017 4:51	59	13/4/2017 5:56	52	14/4/2017 23:01	62	16/4/2017 0:06	57
10/4/2017 2:46	60	11/4/2017 3:51	59	12/4/2017 4:56	60	13/4/2017 6:01	62	14/4/2017 23:06	59	16/4/2017 0:11	56
10/4/2017 2:51	58	11/4/2017 3:56	59	12/4/2017 5:01	60	13/4/2017 6:06	46	14/4/2017 23:11	60	16/4/2017 0:16	54
10/4/2017 2:56	59	11/4/2017 4:01	58	12/4/2017 5:06	61	13/4/2017 6:11	56	14/4/2017 23:16	58	16/4/2017 0:21	61
10/4/2017 3:01	58	11/4/2017 4:06	60	12/4/2017 5:11	60	13/4/2017 6:16	56	14/4/2017 23:21	61	16/4/2017 0:26	63
10/4/2017 3:06	58	11/4/2017 4:11	58	12/4/2017 5:16	61	13/4/2017 6:21	64	14/4/2017 23:26	58	16/4/2017 0:31	46
10/4/2017 3:11	58	11/4/2017 4:16	58	12/4/2017 5:21	60	13/4/2017 6:26	59	14/4/2017 23:31	60	16/4/2017 0:36	63
10/4/2017 3:16	58	11/4/2017 4:21	59	12/4/2017 5:26	62	13/4/2017 6:31	60	14/4/2017 23:36	59	16/4/2017 0:41	48
10/4/2017 3:21	59	11/4/2017 4:26	60	12/4/2017 5:31	62	13/4/2017 6:36	60	14/4/2017 23:41	59	16/4/2017 0:46	63
10/4/2017 3:26	57	11/4/2017 4:31	59	12/4/2017 5:36	62	13/4/2017 6:41	62	14/4/2017 23:46	58	16/4/2017 0:51	63
10/4/2017 3:31	60	11/4/2017 4:36	59	12/4/2017 5:41	62	13/4/2017 6:46	63	14/4/2017 23:51	56	16/4/2017 0:56	63
10/4/2017 3:36	57	11/4/2017 4:41	59	12/4/2017 5:46	61	13/4/2017 6:51	63	14/4/2017 23:56	58	16/4/2017 1:01	45
10/4/2017 3:41	60	11/4/2017 4:46	59	12/4/2017 5:51	62	13/4/2017 6:56	63	15/4/2017 0:01	48	16/4/2017 1:06	62
10/4/2017 3:46	60	11/4/2017 4:51	59	12/4/2017 5:56	62	13/4/2017 23:01	63	15/4/2017 0:06	55	16/4/2017 1:11	58
10/4/2017 3:51	59	11/4/2017 4:56	59	12/4/2017 6:01	62	13/4/2017 23:06	62	15/4/2017 0:11	53	16/4/2017 1:16	55
10/4/2017 3:56	59	11/4/2017 5:01	60	12/4/2017 6:06	62	13/4/2017 23:11	60	15/4/2017 0:16	50	16/4/2017 1:21	62
10/4/2017 4:01	59	11/4/2017 5:06	59	12/4/2017 6:11	63	13/4/2017 23:16	60	15/4/2017 0:21	37	16/4/2017 1:26	62
10/4/2017 4:06	58	11/4/2017 5:11	60	12/4/2017 6:16	51	13/4/2017 23:21	61	15/4/2017 0:26	63	16/4/2017 1:31	52
10/4/2017 4:11	59	11/4/2017 5:16	59	12/4/2017 6:21	57	13/4/2017 23:26	61	15/4/2017 0:31	57	16/4/2017 1:36	53
10/4/2017 4:16	58	11/4/2017 5:21	60	12/4/2017 6:26	58	13/4/2017 23:31	60	15/4/2017 0:36	63	16/4/2017 1:41	63
10/4/2017 4:21	58	11/4/2017 5:26	61	12/4/2017 6:31	57	13/4/2017 23:36	60	15/4/2017 0:41	46	16/4/2017 1:46	63
10/4/2017 4:26	59	11/4/2017 5:31	61	12/4/2017 6:36	60	13/4/2017 23:41	61	15/4/2017 0:46	46	16/4/2017 1:51	62
10/4/2017 4:31	58	11/4/2017 5:36	61	12/4/2017 6:41	60	13/4/2017 23:46	60	15/4/2017 0:51	63	16/4/2017 1:56	62
10/4/2017 4:36	58	11/4/2017 5:41	62	12/4/2017 6:46	63	13/4/2017 23:51	59	15/4/2017 0:56	62	16/4/2017 2:01	61
10/4/2017 4:41	60	11/4/2017 5:46	61	12/4/2017 6:51	63	13/4/2017 23:56	60	15/4/2017 1:01	63	16/4/2017 2:06	62
10/4/2017 4:46	57	11/4/2017 5:51	62	12/4/2017 6:56	63	14/4/2017 0:01	62	15/4/2017 1:06	62	16/4/2017 2:11	62
10/4/2017 4:51	59	11/4/2017 5:56	62	12/4/2017 23:01	60	14/4/2017 0:06	58	15/4/2017 1:11	65	16/4/2017 2:16	63
10/4/2017 4:56	59	11/4/2017 6:01	62	12/4/2017 23:06	61	14/4/2017 0:11	56	15/4/2017 1:16	63	16/4/2017 2:21	62
10/4/2017 5:01	59	11/4/2017 6:06	63	12/4/2017 23:11	63	14/4/2017 0:16	61	15/4/2017 1:21	51	16/4/2017 2:26	62
10/4/2017 5:06	60	11/4/2017 6:11	63	12/4/2017 23:16	61	14/4/2017 0:21	57	15/4/2017 1:26	63	16/4/2017 2:31	61
10/4/2017 5:11	60	11/4/2017 6:16	54	12/4/2017 23:21	61	14/4/2017 0:26	61	15/4/2017 1:31	61	16/4/2017 2:36	61
10/4/2017 5:16	60	11/4/2017 6:21	57	12/4/2017 23:26	60	14/4/2017 0:31	56	15/4/2017 1:36	62	16/4/2017 2:41	62
10/4/2017 5:21	60	11/4/2017 6:26	60	12/4/2017 23:31	62	14/4/2017 0:36	58	15/4/2017 1:41	62	16/4/2017 2:46	61
10/4/2017 5:26	60	11/4/2017 6:31	60	12/4/2017 23:36	61	14/4/2017 0:41	57	15/4/2017 1:46	62	16/4/2017 2:51	62
10/4/2017 5:31	61	11/4/2017 6:36	61	12/4/2017 23:41	59	14/4/2017 0:46	57	15/4/2017 1:51	62	16/4/2017 2:56	61
10/4/2017 5:36	61	11/4/2017 6:41	61	12/4/2017 23:46	59	14/4/2017 0:51	57	15/4/2017 1:56	61	16/4/2017 3:01	61
10/4/2017 5:41	61	11/4/2017 6:46	63	12/4/2017 23:51	62	14/4/2017 0:56	59	15/4/2017 2:01	61	16/4/2017 3:06	60
10/4/2017 5:46	60	11/4/2017 6:51	61	12/4/2017 23:56	60	14/4/2017 1:01	54	15/4/2017 2:06	62	16/4/2017 3:11	60
10/4/2017 5:51	62	11/4/2017 6:56	63	13/4/2017 0:01	59	14/4/2017 1:06	57	15/4/2017 2:11	61	16/4/2017 3:16	62
10/4/2017 5:56	61	11/4/2017 23:01	60	13/4/2017 0:06	57	14/4/2017 1:11	56	15/4/2017 2:16	61	16/4/2017 3:21	61
10/4/2017 6:01	62	11/4/2017 23:06	54	13/4/2017 0:11	60	14/4/2017 1:16	63	15/4/2017 2:21	62	16/4/2017 3:26	60
10/4/2017 6:06	62	11/4/2017 23:11	58	13/4/2017 0:16	59	14/4/2017 1:21	50	15/4/2017 2:26	61	16/4/2017 3:31	60
10/4/2017 6:11	63	11/4/2017 23:16	60	13/4/2017 0:21	59	14/4/2017 1:26	50	15/4/2017 2:31	62	16/4/2017 3:36	62
10/4/2017 6:16	40	11/4/2017 23:21	58	13/4/2017 0:26	60	14/4/2017 1:31	55	15/4/2017 2:36	62	16/4/2017 3:41	61
10/4/2017 6:21	55	11/4/2017 23:26	56	13/4/2017 0:31	56	14/4/2017 1:36	58	15/4/2017 2:41	62	16/4/2017 3:46	60
10/4/2017 6:26	52	11/4/2017 23:31	56	13/4/2017 0:36	57	14/4/2017 1:41	57	15/4/2017 2:46	61	16/4/2017 3:51	61
10/4/2017 6:31	59	11/4/2017 23:36	51	13/4/2017 0:41	54	14/4/2017 1:46	48	15/4/2017 2:51	61	16/4/2017 3:56	60
10/4/2017 6:36	59	11/4/2017 23:41	54	13/4/2017 0:46	60	14/4/2017 1:51	48	15/4/2017 2:56	61	16/4/2017 4:01	61
10/4/2017 6:41	61	11/4/2017 23:46	51	13/4/2017 0:51	62	14/4/2017 1:56	63	15/4/2017 3:01	61	16/4/2017 4:06	60
10/4/2017 6:46	60	11/4/2017 23:51	54	13/4/2017 0:56	54	14/4/2017 2:01	54	15/4/2017 3:06	61	16/4/2017 4:11	61
10/4/2017 6:51	63	11/4/2017 23:56	54	13/4/2017 1:01	63	14/4/2017 2:06	54	15/4/2017 3:11	60	16/4/2017 4:16	60
10/4/2017 6:56	62	12/4/2017 0:01	49	13/4/2017 1:06	63	14/4/2017 2:11	52	15/4/2017 3:16	60	16/4/2017 4:21	61
10/4/2017 23:01	50	12/4/2017 0:06	50	13/4/2017 1:11	53	14/4/2017 2:16	63	15/4/2017 3:21	61	16/4/2017 4:26	61
10/4/2017 23:06	63	12/4/2017 0:11	63	13/4/2017 1:16	63	14/4/2017 2:21	63	15/4/2017 3:26	60	16/4/2017 4:31	60
10/4/2017 23:11	56	12/4/2017 0:16	52	13/4/2017 1:21	62	14/4/2017 2:26	63	15/4/2017 3:31	60	16/4/2017 4:36	60
10/4/2017 23:16	63	12/4/2017 0:21	63	13/4/2017 1:26	49	14/4/2017 2:31	63	15/4/2017 3:36	60	16/4/2017 4:41	60
10/4/2017 23:21	63	12/4/2017 0:26	63	13/4/2017 1:31	63	14/4/2017 2:36	62	15/4/2017 3:41	61	16/4/2017 4:46	60
10/4/2017 23:26	37	12/4/2017 0:31	63	13/4/2017 1:36	63	14/4/2017 2:41	63	15/4/2017 3:46	61	16/4/2017 4:51	59
10/4/2017 23:31	63	12/4/2017 0:36	63	13/4/2017 1:41	60	14/4/2017 2:46	62	15/4/2017 3:51	61	16/4/2017 4:56	62
10/4/2017 23:36	46	12/4/2017 0:41	63	13/4/2017 1:46	55	14/4/2017 2:51	63	15/4/2017 3:56	61	16/4/2017 5:01	61
10/4/2017 23:41	63	12/4/2017 0:46	62	13/4/2017 1:51	62	14/4/2017 2:56	63	15/4/2017 4:01	60	16/4/2017 5:06	62
10/4/2017 23:46	63	12/4/2017 0:51	63	13/4/2017 1:56	62	14/4/2017 3:01	62	15/4/2017 4:06	60	16/4/2017 5:11	60
10/4/2017 23:51	47	12/4/2017 0:56	62	13/4/2017 2:01	62	14/4/2017 3:06	54	15/4/2017 4:11	61	16/4/2017 5:16	60
10/4/2017 23:56	63	12/4/2017 1:01	63	13/4/2017 2:06	63	14/4/2017 3:11	63	15/4/2017 4:16	59	16/4/2017 5:21	61
11/4/2017 0:01	62	12/4/2017 1:06	63	13/4/2017 2:11	62	14/4/2017 3:16	62	15/4/2017 4:21	61	16/4/2017 5:26	61
11/4/2017 0:06	62	12/4/2017 1:11	62	13/4/2017 2:16	63	14/4/2017 3:21	61	15/4/2017 4:26	63	16/4/2017 5:31	61
11/4/2017 0:11	62	12/4/2017 1:16	62	13/4/2017 2:21	60	14/4/2017 3:26	62	15/4/2017 4:31	61	16/4/2017 5:36	61
11/4/2017 0:16	63	12/4/2017 1:21	61	13/4/2017 2:26	62	14/4/2017 3:31	63	15/4/2017 4:36	61	16/4/2017 5:41	60
11/4/2017 0:21	62	12/4/2017 1:26	62	13/4/2017 2:31	60	14/4/2017 3:36	62	15/4/2017 4:41	60	16/4/2017 5:46	61
11/4/2017 0:26	61	12/4/2017 1:31	61	13/4/2017 2:36	61	14/4/2017 3:41	62	15/4/2017 4:46	61	16/4/2017 5:51	62
11/4/2017 0:31	62	12/4/2017 1:36	61	13/4/2017 2:41	62	14/4/2017 3:46	61	15/4/2017 4:51	62	16/4/2017 5:56	62
11/4/2017 0:36	62	12/4/2017 1:41	62	13/4/2017 2:46	61	14/4/2017 3:51	61	15/4/2017 4:56	61	16/4/2017 6:01	63
11/4/2017 0:41	62	12/4/2017 1:46	61	13/4/2017 2:51	60	14/4/2017 3:56	61	15/4/2017 5:01	61	16/4/2017 6:06	46
11/4/2017 0:46	61	12/4/2017 1:51	61	13/4/2017 2:56	60	14/4/2017 4:01	62	15/4/2017 5:06	62	16/4/2017 6:11	63
11/4/2017 0:51	62	12/4/2017 1:56	61	13/4/2017 3:01	62	14/4/2017 4:06	62	15/4/2017 5:11	61	16/4/2017 6:16	63
11/4/2017 0:56	61	12/4/2017 2:01	60	13/4/2017 3:06	60	14/4					

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
17/4/2017 1:11	63	18/4/2017 2:16	60	19/4/2017 3:21	58	20/4/2017 4:26	59	21/4/2017 5:31	61	22/4/2017 6:36	58
17/4/2017 1:16	62	18/4/2017 2:21	60	19/4/2017 3:26	58	20/4/2017 4:31	59	21/4/2017 5:36	61	22/4/2017 6:41	59
17/4/2017 1:21	62	18/4/2017 2:26	61	19/4/2017 3:31	59	20/4/2017 4:36	61	21/4/2017 5:41	61	22/4/2017 6:46	61
17/4/2017 1:26	63	18/4/2017 2:31	60	19/4/2017 3:36	60	20/4/2017 4:41	59	21/4/2017 5:46	63	22/4/2017 6:51	63
17/4/2017 1:31	62	18/4/2017 2:36	60	19/4/2017 3:41	61	20/4/2017 4:46	60	21/4/2017 5:51	62	22/4/2017 6:56	62
17/4/2017 1:36	62	18/4/2017 2:41	60	19/4/2017 3:46	60	20/4/2017 4:51	60	21/4/2017 5:56	62	22/4/2017 23:01	61
17/4/2017 1:41	62	18/4/2017 2:46	58	19/4/2017 3:51	59	20/4/2017 4:56	60	21/4/2017 6:01	62	22/4/2017 23:06	60
17/4/2017 1:46	62	18/4/2017 2:51	60	19/4/2017 3:56	59	20/4/2017 5:01	59	21/4/2017 6:06	54	22/4/2017 23:11	62
17/4/2017 1:51	60	18/4/2017 2:56	58	19/4/2017 4:01	58	20/4/2017 5:06	59	21/4/2017 6:11	63	22/4/2017 23:16	61
17/4/2017 1:56	62	18/4/2017 3:01	59	19/4/2017 4:06	60	20/4/2017 5:11	60	21/4/2017 6:16	55	22/4/2017 23:21	62
17/4/2017 2:01	62	18/4/2017 3:06	58	19/4/2017 4:11	60	20/4/2017 5:16	61	21/4/2017 6:21	58	22/4/2017 23:26	60
17/4/2017 2:06	61	18/4/2017 3:11	59	19/4/2017 4:16	59	20/4/2017 5:21	60	21/4/2017 6:26	59	22/4/2017 23:31	60
17/4/2017 2:11	62	18/4/2017 3:16	58	19/4/2017 4:21	59	20/4/2017 5:26	61	21/4/2017 6:31	61	22/4/2017 23:36	62
17/4/2017 2:16	62	18/4/2017 3:21	57	19/4/2017 4:26	58	20/4/2017 5:31	62	21/4/2017 6:36	62	22/4/2017 23:41	60
17/4/2017 2:21	61	18/4/2017 3:26	58	19/4/2017 4:31	61	20/4/2017 5:36	61	21/4/2017 6:41	63	22/4/2017 23:46	58
17/4/2017 2:26	62	18/4/2017 3:31	59	19/4/2017 4:36	60	20/4/2017 5:41	62	21/4/2017 6:46	62	22/4/2017 23:51	59
17/4/2017 2:31	63	18/4/2017 3:36	59	19/4/2017 4:41	59	20/4/2017 5:46	61	21/4/2017 6:51	63	22/4/2017 23:56	60
17/4/2017 2:36	62	18/4/2017 3:41	58	19/4/2017 4:46	58	20/4/2017 5:51	61	21/4/2017 6:56	62	23/4/2017 0:01	60
17/4/2017 2:41	61	18/4/2017 3:46	60	19/4/2017 4:51	58	20/4/2017 5:56	62	21/4/2017 23:01	63	23/4/2017 0:06	61
17/4/2017 2:46	61	18/4/2017 3:51	59	19/4/2017 4:56	60	20/4/2017 6:01	63	21/4/2017 23:06	63	23/4/2017 0:11	58
17/4/2017 2:51	61	18/4/2017 3:56	57	19/4/2017 5:01	58	20/4/2017 6:06	63	21/4/2017 23:11	61	23/4/2017 0:16	57
17/4/2017 2:56	61	18/4/2017 4:01	58	19/4/2017 5:06	59	20/4/2017 6:11	50	21/4/2017 23:16	62	23/4/2017 0:21	58
17/4/2017 3:01	60	18/4/2017 4:06	59	19/4/2017 5:11	61	20/4/2017 6:16	59	21/4/2017 23:21	62	23/4/2017 0:26	59
17/4/2017 3:06	62	18/4/2017 4:11	59	19/4/2017 5:16	60	20/4/2017 6:21	59	21/4/2017 23:26	61	23/4/2017 0:31	58
17/4/2017 3:11	59	18/4/2017 4:16	59	19/4/2017 5:21	59	20/4/2017 6:26	58	21/4/2017 23:31	60	23/4/2017 0:36	60
17/4/2017 3:16	60	18/4/2017 4:21	58	19/4/2017 5:26	60	20/4/2017 6:31	60	21/4/2017 23:36	62	23/4/2017 0:41	60
17/4/2017 3:21	61	18/4/2017 4:26	59	19/4/2017 5:31	61	20/4/2017 6:36	60	21/4/2017 23:41	61	23/4/2017 0:46	56
17/4/2017 3:26	59	18/4/2017 4:31	59	19/4/2017 5:36	61	20/4/2017 6:41	61	21/4/2017 23:46	62	23/4/2017 0:51	48
17/4/2017 3:31	60	18/4/2017 4:36	60	19/4/2017 5:41	62	20/4/2017 6:46	62	21/4/2017 23:51	60	23/4/2017 0:56	55
17/4/2017 3:36	59	18/4/2017 4:41	58	19/4/2017 5:46	62	20/4/2017 6:51	63	21/4/2017 23:56	61	23/4/2017 1:01	49
17/4/2017 3:41	59	18/4/2017 4:46	59	19/4/2017 5:51	56	20/4/2017 6:56	62	22/4/2017 0:01	56	23/4/2017 1:06	52
17/4/2017 3:46	59	18/4/2017 4:51	60	19/4/2017 5:56	63	20/4/2017 23:01	60	22/4/2017 0:06	62	23/4/2017 1:11	43
17/4/2017 3:51	60	18/4/2017 4:56	60	19/4/2017 6:01	63	20/4/2017 23:06	60	22/4/2017 0:11	58	23/4/2017 1:16	63
17/4/2017 3:56	60	18/4/2017 5:01	59	19/4/2017 6:06	63	20/4/2017 23:11	60	22/4/2017 0:16	56	23/4/2017 1:21	63
17/4/2017 4:01	59	18/4/2017 5:06	59	19/4/2017 6:11	60	20/4/2017 23:16	62	22/4/2017 0:21	37	23/4/2017 1:26	63
17/4/2017 4:06	59	18/4/2017 5:11	60	19/4/2017 6:16	54	20/4/2017 23:21	61	22/4/2017 0:26	62	23/4/2017 1:31	54
17/4/2017 4:11	60	18/4/2017 5:16	60	19/4/2017 6:21	62	20/4/2017 23:26	60	22/4/2017 0:31	62	23/4/2017 1:36	62
17/4/2017 4:16	60	18/4/2017 5:21	60	19/4/2017 6:26	59	20/4/2017 23:31	58	22/4/2017 0:36	62	23/4/2017 1:41	63
17/4/2017 4:21	60	18/4/2017 5:26	60	19/4/2017 6:31	60	20/4/2017 23:36	59	22/4/2017 0:41	62	23/4/2017 1:46	63
17/4/2017 4:26	60	18/4/2017 5:31	61	19/4/2017 6:36	60	20/4/2017 23:41	60	22/4/2017 0:46	63	23/4/2017 1:51	62
17/4/2017 4:31	61	18/4/2017 5:36	61	19/4/2017 6:41	62	20/4/2017 23:46	59	22/4/2017 0:51	62	23/4/2017 1:56	62
17/4/2017 4:36	60	18/4/2017 5:41	61	19/4/2017 6:46	62	20/4/2017 23:51	58	22/4/2017 0:56	63	23/4/2017 2:01	62
17/4/2017 4:41	60	18/4/2017 5:46	61	19/4/2017 6:51	62	20/4/2017 23:56	58	22/4/2017 1:01	62	23/4/2017 2:06	63
17/4/2017 4:46	60	18/4/2017 5:51	63	19/4/2017 6:56	63	21/4/2017 0:01	59	22/4/2017 1:06	62	23/4/2017 2:11	62
17/4/2017 4:51	60	18/4/2017 5:56	62	19/4/2017 23:01	60	21/4/2017 0:06	56	22/4/2017 1:11	62	23/4/2017 2:16	63
17/4/2017 4:56	60	18/4/2017 6:01	62	19/4/2017 23:06	58	21/4/2017 0:11	56	22/4/2017 1:16	62	23/4/2017 2:21	62
17/4/2017 5:01	61	18/4/2017 6:06	63	19/4/2017 23:11	60	21/4/2017 0:16	63	22/4/2017 1:21	62	23/4/2017 2:26	62
17/4/2017 5:06	60	18/4/2017 6:11	50	19/4/2017 23:16	59	21/4/2017 0:21	37	22/4/2017 1:26	62	23/4/2017 2:31	62
17/4/2017 5:11	60	18/4/2017 6:16	57	19/4/2017 23:21	58	21/4/2017 0:26	62	22/4/2017 1:31	62	23/4/2017 2:36	62
17/4/2017 5:16	61	18/4/2017 6:21	59	19/4/2017 23:26	57	21/4/2017 0:31	62	22/4/2017 1:36	62	23/4/2017 2:41	63
17/4/2017 5:21	61	18/4/2017 6:26	58	19/4/2017 23:31	57	21/4/2017 0:36	61	22/4/2017 1:41	61	23/4/2017 2:46	47
17/4/2017 5:26	62	18/4/2017 6:31	61	19/4/2017 23:36	56	21/4/2017 0:41	62	22/4/2017 1:46	61	23/4/2017 2:51	62
17/4/2017 5:31	60	18/4/2017 6:36	60	19/4/2017 23:41	56	21/4/2017 0:46	61	22/4/2017 1:51	62	23/4/2017 2:56	62
17/4/2017 5:36	60	18/4/2017 6:41	63	19/4/2017 23:46	57	21/4/2017 0:51	61	22/4/2017 1:56	61	23/4/2017 3:01	58
17/4/2017 5:41	62	18/4/2017 6:46	63	19/4/2017 23:51	56	21/4/2017 0:56	61	22/4/2017 2:01	62	23/4/2017 3:06	40
17/4/2017 5:46	61	18/4/2017 6:51	64	19/4/2017 23:56	59	21/4/2017 1:01	61	22/4/2017 2:06	61	23/4/2017 3:11	61
17/4/2017 5:51	62	18/4/2017 6:56	66	20/4/2017 0:01	55	21/4/2017 1:06	61	22/4/2017 2:11	61	23/4/2017 3:16	61
17/4/2017 5:56	61	18/4/2017 23:01	63	20/4/2017 0:06	58	21/4/2017 1:11	61	22/4/2017 2:16	62	23/4/2017 3:21	61
17/4/2017 6:01	62	18/4/2017 23:06	58	20/4/2017 0:11	51	21/4/2017 1:16	61	22/4/2017 2:21	61	23/4/2017 3:26	62
17/4/2017 6:06	51	18/4/2017 23:11	58	20/4/2017 0:16	63	21/4/2017 1:21	60	22/4/2017 2:26	62	23/4/2017 3:31	61
17/4/2017 6:11	63	18/4/2017 23:16	59	20/4/2017 0:21	62	21/4/2017 1:26	61	22/4/2017 2:31	63	23/4/2017 3:36	62
17/4/2017 6:16	63	18/4/2017 23:21	56	20/4/2017 0:26	63	21/4/2017 1:31	62	22/4/2017 2:36	62	23/4/2017 3:41	61
17/4/2017 6:21	53	18/4/2017 23:26	55	20/4/2017 0:31	63	21/4/2017 1:36	61	22/4/2017 2:41	61	23/4/2017 3:46	61
17/4/2017 6:26	57	18/4/2017 23:31	56	20/4/2017 0:36	47	21/4/2017 1:41	61	22/4/2017 2:46	61	23/4/2017 3:51	62
17/4/2017 6:31	54	18/4/2017 23:36	54	20/4/2017 0:41	62	21/4/2017 1:46	61	22/4/2017 2:51	60	23/4/2017 3:56	61
17/4/2017 6:36	59	18/4/2017 23:41	57	20/4/2017 0:46	60	21/4/2017 1:51	60	22/4/2017 2:56	60	23/4/2017 4:01	62
17/4/2017 6:41	66	18/4/2017 23:46	57	20/4/2017 0:51	61	21/4/2017 1:56	61	22/4/2017 3:01	60	23/4/2017 4:06	61
17/4/2017 6:46	62	18/4/2017 23:51	52	20/4/2017 0:56	61	21/4/2017 2:01	61	22/4/2017 3:06	60	23/4/2017 4:11	61
17/4/2017 6:51	53	18/4/2017 23:56	56	20/4/2017 1:01	60	21/4/2017 2:06	61	22/4/2017 3:11	54	23/4/2017 4:16	61
17/4/2017 6:56	56	19/4/2017 0:01	57	20/4/2017 1:06	61	21/4/2017 2:11	60	22/4/2017 3:16	65	23/4/2017 4:21	61
17/4/2017 23:01	56	19/4/2017 0:06	51	20/4/2017 1:11	60	21/4/2017 2:16	60	22/4/2017 3:21	60	23/4/2017 4:26	61
17/4/2017 23:06	57	19/4/2017 0:11	63	20/4/2017 1:16	59	21/4/2017 2:21	60	22/4/2017 3:26	60	23/4/2017 4:31	62
17/4/2017 23:11	58	19/4/2017 0:16	55	20/4/2017 1:21	60	21/4/2017 2:26	59	22/4/2017 3:31	61	23/4/2017 4:36	62
17/4/2017 23:16	59	19/4/2017 0:21	49	20/4/2017 1:26	60	21/4/2017 2:31	59	22/4/2017 3:36	60	23/4/2017 4:41	63
17/4/2017 23:21	57	19/4/2017 0:26	63	20/4/2017 1:31	61	21/4/2017 2:36	59	22/4/2017 3:41	60	23/4/2017 4:46	60
17/4/2017 23:26	54	19/4/2017 0:31	55	20/4/2017 1:36	60						

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)	
23/4/2017 23:41	55	25/4/2017 0:46	62
23/4/2017 23:46	55	25/4/2017 0:51	37
23/4/2017 23:51	55	25/4/2017 0:56	48
23/4/2017 23:56	55	25/4/2017 1:01	63
24/4/2017 0:01	62	25/4/2017 1:06	63
24/4/2017 0:06	63	25/4/2017 1:11	62
24/4/2017 0:11	63	25/4/2017 1:16	62
24/4/2017 0:16	62	25/4/2017 1:21	63
24/4/2017 0:21	63	25/4/2017 1:26	62
24/4/2017 0:26	43	25/4/2017 1:31	62
24/4/2017 0:31	63	25/4/2017 1:36	62
24/4/2017 0:36	61	25/4/2017 1:41	61
24/4/2017 0:41	62	25/4/2017 1:46	52
24/4/2017 0:46	61	25/4/2017 1:51	60
24/4/2017 0:51	55	25/4/2017 1:56	60
24/4/2017 0:56	60	25/4/2017 2:01	60
24/4/2017 1:01	61	25/4/2017 2:06	61
24/4/2017 1:06	63	25/4/2017 2:11	60
24/4/2017 1:11	63	25/4/2017 2:16	61
24/4/2017 1:16	62	25/4/2017 2:21	60
24/4/2017 1:21	61	25/4/2017 2:26	61
24/4/2017 1:26	61	25/4/2017 2:31	61
24/4/2017 1:31	60	25/4/2017 2:36	59
24/4/2017 1:36	60	25/4/2017 2:41	60
24/4/2017 1:41	61	25/4/2017 2:46	60
24/4/2017 1:46	60	25/4/2017 2:51	60
24/4/2017 1:51	60	25/4/2017 2:56	59
24/4/2017 1:56	60	25/4/2017 3:01	60
24/4/2017 2:01	61	25/4/2017 3:06	59
24/4/2017 2:06	61	25/4/2017 3:11	58
24/4/2017 2:11	59	25/4/2017 3:16	60
24/4/2017 2:16	60	25/4/2017 3:21	58
24/4/2017 2:21	60	25/4/2017 3:26	59
24/4/2017 2:26	60	25/4/2017 3:31	59
24/4/2017 2:31	59	25/4/2017 3:36	60
24/4/2017 2:36	59	25/4/2017 3:41	60
24/4/2017 2:41	60	25/4/2017 3:46	59
24/4/2017 2:46	59	25/4/2017 3:51	60
24/4/2017 2:51	58	25/4/2017 3:56	60
24/4/2017 2:56	59	25/4/2017 4:01	59
24/4/2017 3:01	60	25/4/2017 4:06	60
24/4/2017 3:06	58	25/4/2017 4:11	59
24/4/2017 3:11	60	25/4/2017 4:16	59
24/4/2017 3:16	58	25/4/2017 4:21	60
24/4/2017 3:21	58	25/4/2017 4:26	60
24/4/2017 3:26	60	25/4/2017 4:31	60
24/4/2017 3:31	59	25/4/2017 4:36	59
24/4/2017 3:36	60	25/4/2017 4:41	59
24/4/2017 3:41	59	25/4/2017 4:46	59
24/4/2017 3:46	58	25/4/2017 4:51	59
24/4/2017 3:51	60	25/4/2017 4:56	59
24/4/2017 3:56	59	25/4/2017 5:01	60
24/4/2017 4:01	59	25/4/2017 5:06	59
24/4/2017 4:06	59	25/4/2017 5:11	61
24/4/2017 4:11	58	25/4/2017 5:16	61
24/4/2017 4:16	60	25/4/2017 5:21	60
24/4/2017 4:21	61	25/4/2017 5:26	61
24/4/2017 4:26	60	25/4/2017 5:31	62
24/4/2017 4:31	60	25/4/2017 5:36	61
24/4/2017 4:36	58	25/4/2017 5:41	62
24/4/2017 4:41	59	25/4/2017 5:46	62
24/4/2017 4:46	59	25/4/2017 5:51	63
24/4/2017 4:51	60	25/4/2017 5:56	64
24/4/2017 4:56	62	25/4/2017 6:01	59
24/4/2017 5:01	59	25/4/2017 6:06	66
24/4/2017 5:06	61	25/4/2017 6:11	60
24/4/2017 5:11	60	25/4/2017 6:16	62
24/4/2017 5:16	61	25/4/2017 6:21	59
24/4/2017 5:21	63	25/4/2017 6:26	59
24/4/2017 5:26	63	25/4/2017 6:31	59
24/4/2017 5:31	62	25/4/2017 6:36	59
24/4/2017 5:36	57	25/4/2017 6:41	63
24/4/2017 5:41	63	25/4/2017 6:46	63
24/4/2017 5:46	62	25/4/2017 6:51	63
24/4/2017 5:51	44	25/4/2017 6:56	63
24/4/2017 5:56	63	25/4/2017 23:01	61
24/4/2017 6:01	63	25/4/2017 23:06	61
24/4/2017 6:06	47	25/4/2017 23:11	62
24/4/2017 6:11	59	25/4/2017 23:16	60
24/4/2017 6:16	59	25/4/2017 23:21	62
24/4/2017 6:21	60	25/4/2017 23:26	61
24/4/2017 6:26	61	25/4/2017 23:31	59
24/4/2017 6:31	63	25/4/2017 23:36	59
24/4/2017 6:36	61	25/4/2017 23:41	57
24/4/2017 6:41	64	25/4/2017 23:46	61
24/4/2017 6:46	63	25/4/2017 23:51	58
24/4/2017 6:51	64	25/4/2017 23:56	60
24/4/2017 6:56	64	26/4/2017 0:01	57
24/4/2017 23:01	61	26/4/2017 0:06	57
24/4/2017 23:06	59	26/4/2017 0:11	54
24/4/2017 23:11	59	26/4/2017 0:16	59
24/4/2017 23:16	60	26/4/2017 0:21	57
24/4/2017 23:21	59	26/4/2017 0:26	52
24/4/2017 23:26	58	26/4/2017 0:31	49
24/4/2017 23:31	58	26/4/2017 0:36	53
24/4/2017 23:36	59	26/4/2017 0:41	63
24/4/2017 23:41	63	26/4/2017 0:46	51
24/4/2017 23:46	58	26/4/2017 0:51	62
24/4/2017 23:51	63	26/4/2017 0:56	54
24/4/2017 23:56	59	26/4/2017 1:01	55
25/4/2017 0:01	57	26/4/2017 1:06	62
25/4/2017 0:06	58	26/4/2017 1:11	63
25/4/2017 0:11	52	26/4/2017 1:16	62
25/4/2017 0:16	53	26/4/2017 1:21	63
25/4/2017 0:21	52	26/4/2017 1:26	62
25/4/2017 0:26	54	26/4/2017 1:31	62
25/4/2017 0:31	48	26/4/2017 1:36	62
25/4/2017 0:36	54	26/4/2017 1:41	62
25/4/2017 0:41	57	26/4/2017 1:46	63

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
Normal Day 07:00-19:00		31/3/2017 13:01	70	7/4/2017 7:31	61	12/4/2017 14:01	65	21/4/2017 8:31	63	26/4/2017 15:01	64
27/3/2017 7:01	60	31/3/2017 13:31	73	7/4/2017 8:01	63	12/4/2017 14:31	65	21/4/2017 9:01	65	26/4/2017 15:31	65
27/3/2017 7:31	60	31/3/2017 14:01	73	7/4/2017 8:31	65	12/4/2017 15:01	66	21/4/2017 9:31	75	26/4/2017 16:01	66
27/3/2017 8:01	60	31/3/2017 14:31	70	7/4/2017 9:01	66	12/4/2017 15:31	65	21/4/2017 10:01	77	26/4/2017 16:31	64
27/3/2017 8:31	62	31/3/2017 15:01	66	7/4/2017 9:31	63	12/4/2017 16:01	66	21/4/2017 10:31	76	26/4/2017 17:01	63
27/3/2017 9:01	63	31/3/2017 15:31	73	7/4/2017 10:01	64	12/4/2017 16:31	66	21/4/2017 11:01	66	26/4/2017 17:31	63
27/3/2017 9:31	66	31/3/2017 16:01	74	7/4/2017 10:31	65	12/4/2017 17:01	64	21/4/2017 11:31	63	26/4/2017 18:01	63
27/3/2017 10:01	65	31/3/2017 16:31	59	7/4/2017 11:01	67	12/4/2017 17:31	63	21/4/2017 12:01	61	26/4/2017 18:31	62
27/3/2017 10:31	65	31/3/2017 17:01	62	7/4/2017 11:31	66	12/4/2017 18:01	62	21/4/2017 12:31	62		
27/3/2017 11:01	65	31/3/2017 17:31	62	7/4/2017 12:01	62	12/4/2017 18:31	61	21/4/2017 13:01	73	Normal Day 19:00-23:00	
27/3/2017 11:31	64	31/3/2017 18:01	62	7/4/2017 12:31	62	13/4/2017 7:01	62	21/4/2017 13:31	66	Sunday & Holiday	
27/3/2017 12:01	61	31/3/2017 18:31	61	7/4/2017 13:01	63	13/4/2017 7:31	62	21/4/2017 14:01	65	07:00-23:00	
27/3/2017 12:31	62	1/4/2017 7:01	62	7/4/2017 13:31	64	13/4/2017 8:01	66	21/4/2017 14:31	65	27/3/2017 19:01	61
27/3/2017 13:01	64	1/4/2017 7:31	63	7/4/2017 14:01	64	13/4/2017 8:31	64	21/4/2017 15:01	64	27/3/2017 19:06	61
27/3/2017 13:31	65	1/4/2017 8:01	62	7/4/2017 14:31	63	13/4/2017 9:01	63	21/4/2017 15:31	64	27/3/2017 19:11	61
27/3/2017 14:01	65	1/4/2017 8:31	63	7/4/2017 15:01	64	13/4/2017 9:31	60	21/4/2017 16:01	58	27/3/2017 19:16	60
27/3/2017 14:31	64	1/4/2017 9:01	65	7/4/2017 15:31	65	13/4/2017 10:01	64	21/4/2017 16:31	66	27/3/2017 19:21	60
27/3/2017 15:01	64	1/4/2017 9:31	63	7/4/2017 16:01	65	13/4/2017 10:31	66	21/4/2017 17:01	63	27/3/2017 19:26	60
27/3/2017 15:31	64	1/4/2017 10:01	63	7/4/2017 16:31	65	13/4/2017 11:01	66	21/4/2017 17:31	62	27/3/2017 19:31	61
27/3/2017 16:01	64	1/4/2017 10:31	65	7/4/2017 17:01	62	13/4/2017 11:31	63	21/4/2017 18:01	61	27/3/2017 19:36	61
27/3/2017 16:31	64	1/4/2017 11:01	66	7/4/2017 17:31	62	13/4/2017 12:01	63	21/4/2017 18:31	59	27/3/2017 19:41	61
27/3/2017 17:01	63	1/4/2017 11:31	64	7/4/2017 18:01	62	13/4/2017 12:31	63	22/4/2017 7:01	60	27/3/2017 19:46	60
27/3/2017 17:31	63	1/4/2017 12:01	61	7/4/2017 18:31	62	13/4/2017 13:01	67	22/4/2017 7:31	61	27/3/2017 19:51	59
27/3/2017 18:01	61	1/4/2017 12:31	61	8/4/2017 7:01	60	13/4/2017 13:31	67	22/4/2017 8:01	62	27/3/2017 19:56	60
27/3/2017 18:31	62	1/4/2017 13:01	63	8/4/2017 7:31	61	13/4/2017 14:01	67	22/4/2017 8:31	64	27/3/2017 20:01	61
28/3/2017 7:01	60	1/4/2017 13:31	64	8/4/2017 8:01	62	13/4/2017 14:31	66	22/4/2017 9:01	66	27/3/2017 20:06	61
28/3/2017 7:31	61	1/4/2017 14:01	63	8/4/2017 8:31	64	13/4/2017 15:01	67	22/4/2017 9:31	65	27/3/2017 20:11	61
28/3/2017 8:01	62	1/4/2017 14:31	65	8/4/2017 9:01	65	13/4/2017 15:31	66	22/4/2017 10:01	64	27/3/2017 20:16	61
28/3/2017 8:31	63	1/4/2017 15:01	63	8/4/2017 9:31	64	13/4/2017 16:01	65	22/4/2017 10:31	64	27/3/2017 20:21	62
28/3/2017 9:01	64	1/4/2017 15:31	66	8/4/2017 10:01	64	13/4/2017 16:31	65	22/4/2017 11:01	65	27/3/2017 20:26	61
28/3/2017 9:31	65	1/4/2017 16:01	68	8/4/2017 10:31	65	13/4/2017 17:01	63	22/4/2017 11:31	63	27/3/2017 20:31	60
28/3/2017 10:01	67	1/4/2017 16:31	64	8/4/2017 11:01	64	13/4/2017 17:31	61	22/4/2017 12:01	62	27/3/2017 20:36	60
28/3/2017 10:31	68	1/4/2017 17:01	62	8/4/2017 11:31	63	13/4/2017 18:01	61	22/4/2017 12:31	64	27/3/2017 20:41	60
28/3/2017 11:01	67	1/4/2017 17:31	62	8/4/2017 12:01	61	13/4/2017 18:31	61	22/4/2017 13:01	64	27/3/2017 20:46	60
28/3/2017 11:31	63	1/4/2017 18:01	61	8/4/2017 12:31	62	18/4/2017 7:01	62	22/4/2017 13:31	65	27/3/2017 20:51	60
28/3/2017 12:01	61	1/4/2017 18:31	60	8/4/2017 13:01	64	18/4/2017 7:31	62	22/4/2017 14:01	64	27/3/2017 20:56	60
28/3/2017 12:31	62	3/4/2017 7:01	62	8/4/2017 13:31	66	18/4/2017 8:01	62	22/4/2017 14:31	65	27/3/2017 21:01	61
28/3/2017 13:01	65	3/4/2017 7:31	62	8/4/2017 14:01	66	18/4/2017 8:31	66	22/4/2017 15:01	65	27/3/2017 21:06	61
28/3/2017 13:31	65	3/4/2017 8:01	62	8/4/2017 14:31	67	18/4/2017 9:01	68	22/4/2017 15:31	64	27/3/2017 21:11	61
28/3/2017 14:01	64	3/4/2017 8:31	67	8/4/2017 15:01	68	18/4/2017 9:31	67	22/4/2017 16:01	64	27/3/2017 21:16	60
28/3/2017 14:31	64	3/4/2017 9:01	65	8/4/2017 15:31	66	18/4/2017 10:01	65	22/4/2017 16:31	65	27/3/2017 21:21	60
28/3/2017 15:01	63	3/4/2017 9:31	63	8/4/2017 16:01	66	18/4/2017 10:31	66	22/4/2017 17:01	62	27/3/2017 21:26	60
28/3/2017 15:31	64	3/4/2017 10:01	63	8/4/2017 16:31	66	18/4/2017 11:01	66	22/4/2017 17:31	63	27/3/2017 21:31	61
28/3/2017 16:01	64	3/4/2017 10:31	66	8/4/2017 17:01	63	18/4/2017 11:31	64	22/4/2017 18:01	62	27/3/2017 21:36	60
28/3/2017 16:31	64	3/4/2017 11:01	68	8/4/2017 17:31	64	18/4/2017 12:01	62	22/4/2017 18:31	61	27/3/2017 21:41	61
28/3/2017 17:01	63	3/4/2017 11:31	63	8/4/2017 18:01	62	18/4/2017 12:31	63	24/4/2017 7:01	60	27/3/2017 21:46	61
28/3/2017 17:31	63	3/4/2017 12:01	60	8/4/2017 18:31	62	18/4/2017 13:01	65	24/4/2017 7:31	61	27/3/2017 21:51	62
28/3/2017 18:01	62	3/4/2017 12:31	62	10/4/2017 7:01	61	18/4/2017 13:31	66	24/4/2017 8:01	63	27/3/2017 21:56	60
28/3/2017 18:31	61	3/4/2017 13:01	66	10/4/2017 7:31	61	18/4/2017 14:01	68	24/4/2017 8:31	64	27/3/2017 22:01	59
29/3/2017 7:01	60	3/4/2017 13:31	65	10/4/2017 8:01	65	18/4/2017 14:31	66	24/4/2017 9:01	65	27/3/2017 22:06	60
29/3/2017 7:31	61	3/4/2017 14:01	66	10/4/2017 8:31	66	18/4/2017 15:01	65	24/4/2017 9:31	65	27/3/2017 22:11	60
29/3/2017 8:01	61	3/4/2017 14:31	72	10/4/2017 9:01	66	18/4/2017 15:31	66	24/4/2017 10:01	66	27/3/2017 22:16	61
29/3/2017 8:31	64	3/4/2017 15:01	70	10/4/2017 9:31	65	18/4/2017 16:01	68	24/4/2017 10:31	68	27/3/2017 22:21	60
29/3/2017 9:01	64	3/4/2017 15:31	63	10/4/2017 10:01	65	18/4/2017 16:31	64	24/4/2017 11:01	68	27/3/2017 22:26	60
29/3/2017 9:31	66	3/4/2017 16:01	63	10/4/2017 10:31	66	18/4/2017 17:01	63	24/4/2017 11:31	64	27/3/2017 22:31	60
29/3/2017 10:01	67	3/4/2017 16:31	64	10/4/2017 11:01	66	18/4/2017 17:31	63	24/4/2017 12:01	63	27/3/2017 22:36	60
29/3/2017 10:31	67	3/4/2017 17:01	63	10/4/2017 11:31	63	18/4/2017 18:01	63	24/4/2017 12:31	63	27/3/2017 22:41	59
29/3/2017 11:01	66	3/4/2017 17:31	63	10/4/2017 12:01	61	18/4/2017 18:31	63	24/4/2017 13:01	66	27/3/2017 22:46	60
29/3/2017 11:31	64	3/4/2017 18:01	63	10/4/2017 12:31	62	19/4/2017 7:01	62	24/4/2017 13:31	67	27/3/2017 22:51	59
29/3/2017 12:01	62	3/4/2017 18:31	61	10/4/2017 13:01	63	19/4/2017 7:31	63	24/4/2017 14:01	65	27/3/2017 22:56	59
29/3/2017 12:31	62	5/4/2017 7:01	60	10/4/2017 13:31	66	19/4/2017 8:01	62	24/4/2017 14:31	66	28/3/2017 19:01	61
29/3/2017 13:01	65	5/4/2017 7:31	62	10/4/2017 14:01	67	19/4/2017 8:31	62	24/4/2017 15:01	67	28/3/2017 19:06	61
29/3/2017 13:31	65	5/4/2017 8:01	61	10/4/2017 14:31	67	19/4/2017 9:01	68	24/4/2017 15:31	67	28/3/2017 19:11	61
29/3/2017 14:01	65	5/4/2017 8:31	71	10/4/2017 15:01	67	19/4/2017 9:31	70	24/4/2017 16:01	65	28/3/2017 19:16	60
29/3/2017 14:31	66	5/4/2017 9:01	73	10/4/2017 15:31	66	19/4/2017 10:01	73	24/4/2017 16:31	64	28/3/2017 19:21	62
29/3/2017 15:01	60	5/4/2017 9:31	72	10/4/2017 16:01	67	19/4/2017 10:31	64	24/4/2017 17:01	65	28/3/2017 19:26	61
29/3/2017 15:31	67	5/4/2017 10:01	73	10/4/2017 16:31	66	19/4/2017 11:01	65	24/4/2017 17:31	63	28/3/2017 19:31	62
29/3/2017 16:01	68	5/4/2017 10:31	64	10/4/2017 17:01	64	19/4/2017 11:31	64	24/4/2017 18:01	62	28/3/2017 19:36	62
29/3/2017 16:31	66	5/4/2017 11:01	71	10/4/2017 17:31	63	19/4/2017 12:01	62	24/4/2017 18:31	62	28/3/2017 19:41	61
29/3/2017 17:01	63	5/4/2017 11:31	63	10/4/2017 18:01	61	19/4/2017 12:31	61	25/4/2017 7:01	61	28/3/2017 19:46	62
29/3/2017 17:31	61	5/4/2017 12:01	61	10/4/2017 18:31	60	19/4/2017 13:01	65	25/4/2017 7:31	61	28/3/2017 19:51	54
29/3/2017 18:01	60	5/4/2017 12:31	63	11/4/2017 7:01	62	19/4/2017 13:31	66	25/4/2017 8:01	60	28/3/2017 19:56	62
29/3/2017 18:31	59	5/4/2017 13:01	68	11/4/2017 7:31	62	19/4/2017 14:01	64	25/4/2017 8:31	63	28/3/2017 20:01	62
30/3/2017 7:01	60	5/4/2017 13:31	65	11/4/2017 8:01	62	19/4/2017 14:31	63	25/4/2017 9:01	65	28/3/2017 20:06	

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)							
29/3/2017 19:01	60	31/3/2017 20:06	62	2/4/2017 9:11	61	2/4/2017 18:16	46	4/4/2017 7:21	58
29/3/2017 19:06	60	31/3/2017 20:11	62	2/4/2017 9:16	61	2/4/2017 18:21	61	4/4/2017 7:26	59
29/3/2017 19:11	63	31/3/2017 20:16	63	2/4/2017 9:21	61	2/4/2017 18:26	61	4/4/2017 7:31	59
29/3/2017 19:16	61	31/3/2017 20:21	64	2/4/2017 9:26	61	2/4/2017 18:31	61	4/4/2017 7:36	60
29/3/2017 19:21	59	31/3/2017 20:26	62	2/4/2017 9:31	61	2/4/2017 18:36	63	4/4/2017 7:41	60
29/3/2017 19:26	60	31/3/2017 20:31	62	2/4/2017 9:36	61	2/4/2017 18:41	60	4/4/2017 7:46	59
29/3/2017 19:31	62	31/3/2017 20:36	62	2/4/2017 9:41	62	2/4/2017 18:46	62	4/4/2017 7:51	63
29/3/2017 19:36	61	31/3/2017 20:41	62	2/4/2017 9:46	61	2/4/2017 18:51	61	4/4/2017 7:56	60
29/3/2017 19:41	62	31/3/2017 20:46	64	2/4/2017 9:51	62	2/4/2017 18:56	61	4/4/2017 8:01	60
29/3/2017 19:46	61	31/3/2017 20:51	63	2/4/2017 9:56	61	2/4/2017 19:01	61	4/4/2017 8:06	60
29/3/2017 19:51	62	31/3/2017 20:56	62	2/4/2017 10:01	61	2/4/2017 19:06	61	4/4/2017 8:11	61
29/3/2017 19:56	61	31/3/2017 21:01	63	2/4/2017 10:06	61	2/4/2017 19:11	61	4/4/2017 8:16	60
29/3/2017 20:01	61	31/3/2017 21:06	62	2/4/2017 10:11	62	2/4/2017 19:16	60	4/4/2017 8:21	60
29/3/2017 20:06	61	31/3/2017 21:11	62	2/4/2017 10:16	61	2/4/2017 19:21	61	4/4/2017 8:26	60
29/3/2017 20:11	60	31/3/2017 21:16	63	2/4/2017 10:21	61	2/4/2017 19:26	61	4/4/2017 8:31	61
29/3/2017 20:16	63	31/3/2017 21:21	63	2/4/2017 10:26	62	2/4/2017 19:31	60	4/4/2017 8:36	61
29/3/2017 20:21	60	31/3/2017 21:26	63	2/4/2017 10:31	61	2/4/2017 19:36	61	4/4/2017 8:41	60
29/3/2017 20:26	61	31/3/2017 21:31	61	2/4/2017 10:36	61	2/4/2017 19:41	61	4/4/2017 8:46	61
29/3/2017 20:31	60	31/3/2017 21:36	62	2/4/2017 10:41	60	2/4/2017 19:46	60	4/4/2017 8:51	61
29/3/2017 20:36	60	31/3/2017 21:41	62	2/4/2017 10:46	60	2/4/2017 19:51	60	4/4/2017 8:56	61
29/3/2017 20:41	60	31/3/2017 21:46	64	2/4/2017 10:51	60	2/4/2017 19:56	60	4/4/2017 9:01	63
29/3/2017 20:46	61	31/3/2017 21:51	62	2/4/2017 10:56	62	2/4/2017 20:01	60	4/4/2017 9:06	61
29/3/2017 20:51	60	31/3/2017 21:56	58	2/4/2017 11:01	60	2/4/2017 20:06	60	4/4/2017 9:11	61
29/3/2017 20:56	60	31/3/2017 22:01	62	2/4/2017 11:06	60	2/4/2017 20:11	60	4/4/2017 9:16	54
29/3/2017 21:01	60	31/3/2017 22:06	62	2/4/2017 11:11	61	2/4/2017 20:16	61	4/4/2017 9:21	59
29/3/2017 21:06	61	31/3/2017 22:11	57	2/4/2017 11:16	61	2/4/2017 20:21	59	4/4/2017 9:26	64
29/3/2017 21:11	61	31/3/2017 22:16	63	2/4/2017 11:21	60	2/4/2017 20:26	61	4/4/2017 9:31	54
29/3/2017 21:16	61	31/3/2017 22:21	62	2/4/2017 11:26	60	2/4/2017 20:31	60	4/4/2017 9:36	61
29/3/2017 21:21	60	31/3/2017 22:26	60	2/4/2017 11:31	61	2/4/2017 20:36	61	4/4/2017 9:41	63
29/3/2017 21:26	59	31/3/2017 22:31	62	2/4/2017 11:36	61	2/4/2017 20:41	59	4/4/2017 9:46	62
29/3/2017 21:31	59	31/3/2017 22:36	62	2/4/2017 11:41	62	2/4/2017 20:46	60	4/4/2017 9:51	61
29/3/2017 21:36	61	31/3/2017 22:41	62	2/4/2017 11:46	61	2/4/2017 20:51	60	4/4/2017 9:56	48
29/3/2017 21:41	61	31/3/2017 22:46	62	2/4/2017 11:51	60	2/4/2017 20:56	60	4/4/2017 10:01	65
29/3/2017 21:46	60	31/3/2017 22:51	63	2/4/2017 11:56	60	2/4/2017 21:01	61	4/4/2017 10:06	63
29/3/2017 21:51	60	31/3/2017 22:56	61	2/4/2017 12:01	61	2/4/2017 21:06	60	4/4/2017 10:11	63
29/3/2017 21:56	60	1/4/2017 19:01	60	2/4/2017 12:06	61	2/4/2017 21:11	60	4/4/2017 10:16	61
29/3/2017 22:01	60	1/4/2017 19:06	59	2/4/2017 12:11	61	2/4/2017 21:16	61	4/4/2017 10:21	63
29/3/2017 22:06	60	1/4/2017 19:11	60	2/4/2017 12:16	61	2/4/2017 21:21	60	4/4/2017 10:26	61
29/3/2017 22:11	60	1/4/2017 19:16	61	2/4/2017 12:21	61	2/4/2017 21:26	61	4/4/2017 10:31	62
29/3/2017 22:16	60	1/4/2017 19:21	61	2/4/2017 12:26	61	2/4/2017 21:31	60	4/4/2017 10:36	63
29/3/2017 22:21	60	1/4/2017 19:26	61	2/4/2017 12:31	62	2/4/2017 21:36	59	4/4/2017 10:41	62
29/3/2017 22:26	60	1/4/2017 19:31	63	2/4/2017 12:36	63	2/4/2017 21:41	61	4/4/2017 10:46	63
29/3/2017 22:31	60	1/4/2017 19:36	61	2/4/2017 12:41	62	2/4/2017 21:46	60	4/4/2017 10:51	60
29/3/2017 22:36	59	1/4/2017 19:41	62	2/4/2017 12:46	63	2/4/2017 21:51	59	4/4/2017 10:56	63
29/3/2017 22:41	59	1/4/2017 19:46	63	2/4/2017 12:51	61	2/4/2017 21:56	60	4/4/2017 11:01	57
29/3/2017 22:46	61	1/4/2017 19:51	60	2/4/2017 12:56	62	2/4/2017 22:01	59	4/4/2017 11:06	62
29/3/2017 22:51	59	1/4/2017 19:56	60	2/4/2017 13:01	61	2/4/2017 22:06	60	4/4/2017 11:11	65
29/3/2017 22:56	59	1/4/2017 20:01	60	2/4/2017 13:06	61	2/4/2017 22:11	61	4/4/2017 11:16	67
30/3/2017 19:01	62	1/4/2017 20:06	60	2/4/2017 13:11	61	2/4/2017 22:16	59	4/4/2017 11:21	59
30/3/2017 19:06	62	1/4/2017 20:11	60	2/4/2017 13:16	62	2/4/2017 22:21	59	4/4/2017 11:26	63
30/3/2017 19:11	62	1/4/2017 20:16	60	2/4/2017 13:21	61	2/4/2017 22:26	59	4/4/2017 11:31	61
30/3/2017 19:16	62	1/4/2017 20:21	61	2/4/2017 13:26	61	2/4/2017 22:31	59	4/4/2017 11:36	60
30/3/2017 19:21	62	1/4/2017 20:26	61	2/4/2017 13:31	61	2/4/2017 22:36	59	4/4/2017 11:41	49
30/3/2017 19:26	62	1/4/2017 20:31	60	2/4/2017 13:36	62	2/4/2017 22:41	59	4/4/2017 11:46	59
30/3/2017 19:31	61	1/4/2017 20:36	62	2/4/2017 13:41	61	2/4/2017 22:46	59	4/4/2017 11:51	64
30/3/2017 19:36	62	1/4/2017 20:41	60	2/4/2017 13:46	61	2/4/2017 22:51	59	4/4/2017 11:56	62
30/3/2017 19:41	61	1/4/2017 20:46	60	2/4/2017 13:51	61	2/4/2017 22:56	59	4/4/2017 12:01	61
30/3/2017 19:46	61	1/4/2017 20:51	61	2/4/2017 13:56	60	3/4/2017 19:01	61	4/4/2017 12:06	61
30/3/2017 19:51	61	1/4/2017 20:56	61	2/4/2017 14:01	60	3/4/2017 19:06	61	4/4/2017 12:11	61
30/3/2017 19:56	62	1/4/2017 21:01	60	2/4/2017 14:06	61	3/4/2017 19:11	62	4/4/2017 12:16	61
30/3/2017 20:01	62	1/4/2017 21:06	60	2/4/2017 14:11	61	3/4/2017 19:16	62	4/4/2017 12:21	61
30/3/2017 20:06	61	1/4/2017 21:11	61	2/4/2017 14:16	61	3/4/2017 19:21	61	4/4/2017 12:26	60
30/3/2017 20:11	61	1/4/2017 21:16	62	2/4/2017 14:21	61	3/4/2017 19:26	62	4/4/2017 12:31	61
30/3/2017 20:16	61	1/4/2017 21:21	61	2/4/2017 14:26	61	3/4/2017 19:31	61	4/4/2017 12:36	61
30/3/2017 20:21	61	1/4/2017 21:26	60	2/4/2017 14:31	61	3/4/2017 19:36	61	4/4/2017 12:41	61
30/3/2017 20:26	60	1/4/2017 21:31	60	2/4/2017 14:36	61	3/4/2017 19:41	61	4/4/2017 12:46	46
30/3/2017 20:31	62	1/4/2017 21:36	60	2/4/2017 14:41	61	3/4/2017 19:46	61	4/4/2017 12:51	63
30/3/2017 20:36	60	1/4/2017 21:41	61	2/4/2017 14:46	61	3/4/2017 19:51	62	4/4/2017 12:56	62
30/3/2017 20:41	61	1/4/2017 21:46	60	2/4/2017 14:51	61	3/4/2017 19:56	61	4/4/2017 13:01	61
30/3/2017 20:46	62	1/4/2017 21:51	60	2/4/2017 14:56	61	3/4/2017 20:01	60	4/4/2017 13:06	61
30/3/2017 20:51	60	1/4/2017 21:56	60	2/4/2017 15:01	61	3/4/2017 20:06	62	4/4/2017 13:11	61
30/3/2017 20:56	60	1/4/2017 22:01	62	2/4/2017 15:06	62	3/4/2017 20:11	61	4/4/2017 13:16	61
30/3/2017 21:01	61	1/4/2017 22:06	60	2/4/2017 15:11	61	3/4/2017 20:16	60	4/4/2017 13:21	61
30/3/2017 21:06	61	1/4/2017 22:11	60	2/4/2017 15:16	61	3/4/2017 20:21	62	4/4/2017 13:26	63
30/3/2017 21:11	61	1/4/2017 22:16	61	2/4/2017 15:21	60	3/4/2017 20:26	61	4/4/2017 13:31	53
30/3/2017 21:16	61	1/4/2017 22:21	60	2/4/2017 15:26	61	3/4/2017 20:31	60	4/4/2017 13:36	63
30/3/2017 21:21	60	1/4/2017 22:26	60	2/4/2017 15:31	61	3/4/2017 20:36	60	4/4/2017 13:41	55
30/3/2017 21:26	62	1/4/2017 22:31	60	2/4/2017 15:36	61	3/4/2017 20:41	61	4/4/2017 13:46	55
30/3/2017 21:31	60	1/4/2017 22:36	60	2/4/2017 15:41	61	3/4/2017 20:46	60	4/4/2017 13:51	57
30/3/2017 21:36	62	1/4/2017 22:41	60	2/4/2017 15:46	61	3/4/2017 20:51	61	4/4/2017 13:56	64
30/3/2017 21:41	60	1/4/2017 22:46	60	2/4/2017 15:51	61	3/4/2017 20:56	60	4/4/2017 14:01	61
30/3/2017 21:46	60	1/4/2017 22:51	59	2/4/2017 15:56	62	3/4/2017 21:01	61	4/4/2017 14:06	62
30/3/2017 21:51	60	1/4/2017 22:56	59	2/4/2017 16:01	61	3/4/2017 21:06	60	4/4/2017 14:11	63
30/3/2017 21:56	60	2/4/2017 7:01	58	2/4/2017 16:06	61	3/4/2017 21:11	60	4/4/2017 14:16	61
30/3/2017 22:01	60	2/4/2017 7:06	59	2/4/2017 16:11	61	3/4/2017 21:16	60	4/4/2017 14:21	62
30/3/2017 22:06	60	2/4/2017 7:11	59	2/4/2017 16:16	61	3/4/2017 21:21	61	4/4/2017 14:26	62
30/3/2017 22:11	60	2/4/2017 7:16	62	2/4/2017 16:21	61	3/4/2017 21:26	59	4/4/2017 14:31	61
30/3/2017 22:16	60	2/4/2017 7:21	63	2/4/2017 16:26	60	3/4/2017 21:31	60	4/4/2017 14:36	62
30/3/2017 22:21	59	2/4/2017 7:26	61	2/4/2017 16:31	60	3/4/2017 21:36	60	4/4/2017 14:41	62
30/3/2017 22:26	62	2/4/2017 7:31	59	2/4/2017 16:36	61	3/4/2017 21:41	61	4/4/2017 14:46	63

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
5/4/2017 21:31	59	7/4/2017 22:36	60	9/4/2017 11:41	61	9/4/2017 20:46	59	11/4/2017 21:51	60	13/4/2017 22:56	59
5/4/2017 21:36	62	7/4/2017 22:41	62	9/4/2017 11:46	62	9/4/2017 20:51	60	11/4/2017 21:56	59	14/4/2017 7:01	59
5/4/2017 21:41	60	7/4/2017 22:46	60	9/4/2017 11:51	61	9/4/2017 20:56	59	11/4/2017 22:01	59	14/4/2017 7:06	60
5/4/2017 21:46	62	7/4/2017 22:51	60	9/4/2017 11:56	61	9/4/2017 21:01	59	11/4/2017 22:06	60	14/4/2017 7:11	59
5/4/2017 21:51	60	7/4/2017 22:56	59	9/4/2017 12:01	62	9/4/2017 21:06	59	11/4/2017 22:11	60	14/4/2017 7:16	59
5/4/2017 21:56	59	8/4/2017 19:01	61	9/4/2017 12:06	61	9/4/2017 21:11	59	11/4/2017 22:16	60	14/4/2017 7:21	60
5/4/2017 22:01	60	8/4/2017 19:06	60	9/4/2017 12:11	60	9/4/2017 21:16	59	11/4/2017 22:21	60	14/4/2017 7:26	59
5/4/2017 22:06	60	8/4/2017 19:11	62	9/4/2017 12:16	61	9/4/2017 21:21	59	11/4/2017 22:26	60	14/4/2017 7:31	59
5/4/2017 22:11	60	8/4/2017 19:16	61	9/4/2017 12:21	61	9/4/2017 21:26	58	11/4/2017 22:31	60	14/4/2017 7:36	59
5/4/2017 22:16	59	8/4/2017 19:21	62	9/4/2017 12:26	50	9/4/2017 21:31	60	11/4/2017 22:36	60	14/4/2017 7:41	61
5/4/2017 22:21	60	8/4/2017 19:26	61	9/4/2017 12:31	60	9/4/2017 21:36	59	11/4/2017 22:41	59	14/4/2017 7:46	61
5/4/2017 22:26	60	8/4/2017 19:31	61	9/4/2017 12:36	61	9/4/2017 21:41	59	11/4/2017 22:46	60	14/4/2017 7:51	60
5/4/2017 22:31	60	8/4/2017 19:36	64	9/4/2017 12:41	61	9/4/2017 21:46	59	11/4/2017 22:51	60	14/4/2017 7:56	59
5/4/2017 22:36	59	8/4/2017 19:41	62	9/4/2017 12:46	62	9/4/2017 21:51	59	11/4/2017 22:56	60	14/4/2017 8:01	60
5/4/2017 22:41	59	8/4/2017 19:46	62	9/4/2017 12:51	61	9/4/2017 21:56	59	12/4/2017 19:01	63	14/4/2017 8:06	60
5/4/2017 22:46	58	8/4/2017 19:51	61	9/4/2017 12:56	61	9/4/2017 22:01	58	12/4/2017 19:06	63	14/4/2017 8:11	61
5/4/2017 22:51	59	8/4/2017 19:56	61	9/4/2017 13:01	61	9/4/2017 22:06	59	12/4/2017 19:11	56	14/4/2017 8:16	60
5/4/2017 22:56	59	8/4/2017 20:01	61	9/4/2017 13:06	61	9/4/2017 22:11	60	12/4/2017 19:16	63	14/4/2017 8:21	61
6/4/2017 19:01	61	8/4/2017 20:06	61	9/4/2017 13:11	61	9/4/2017 22:16	59	12/4/2017 19:21	63	14/4/2017 8:26	61
6/4/2017 19:06	60	8/4/2017 20:11	60	9/4/2017 13:16	61	9/4/2017 22:21	59	12/4/2017 19:26	63	14/4/2017 8:31	61
6/4/2017 19:11	61	8/4/2017 20:16	61	9/4/2017 13:21	61	9/4/2017 22:26	59	12/4/2017 19:31	63	14/4/2017 8:36	61
6/4/2017 19:16	62	8/4/2017 20:21	61	9/4/2017 13:26	62	9/4/2017 22:31	58	12/4/2017 19:36	62	14/4/2017 8:41	61
6/4/2017 19:21	62	8/4/2017 20:26	60	9/4/2017 13:31	61	9/4/2017 22:36	59	12/4/2017 19:41	63	14/4/2017 8:46	61
6/4/2017 19:26	63	8/4/2017 20:31	61	9/4/2017 13:36	61	9/4/2017 22:41	59	12/4/2017 19:46	63	14/4/2017 8:51	60
6/4/2017 19:31	62	8/4/2017 20:36	61	9/4/2017 13:41	62	9/4/2017 22:46	58	12/4/2017 19:51	63	14/4/2017 8:56	61
6/4/2017 19:36	62	8/4/2017 20:41	60	9/4/2017 13:46	62	9/4/2017 22:51	59	12/4/2017 19:56	63	14/4/2017 9:01	61
6/4/2017 19:41	62	8/4/2017 20:46	61	9/4/2017 13:51	61	9/4/2017 22:56	59	12/4/2017 20:01	62	14/4/2017 9:06	61
6/4/2017 19:46	62	8/4/2017 20:51	60	9/4/2017 13:56	62	10/4/2017 19:01	61	12/4/2017 20:06	62	14/4/2017 9:11	62
6/4/2017 19:51	61	8/4/2017 20:56	60	9/4/2017 14:01	62	10/4/2017 19:06	61	12/4/2017 20:11	63	14/4/2017 9:16	61
6/4/2017 19:56	62	8/4/2017 21:01	60	9/4/2017 14:06	61	10/4/2017 19:11	61	12/4/2017 20:16	63	14/4/2017 9:21	61
6/4/2017 20:01	61	8/4/2017 21:06	60	9/4/2017 14:11	62	10/4/2017 19:16	61	12/4/2017 20:21	62	14/4/2017 9:26	60
6/4/2017 20:06	61	8/4/2017 21:11	60	9/4/2017 14:16	61	10/4/2017 19:21	61	12/4/2017 20:26	62	14/4/2017 9:31	61
6/4/2017 20:11	62	8/4/2017 21:16	63	9/4/2017 14:21	61	10/4/2017 19:26	61	12/4/2017 20:31	63	14/4/2017 9:36	61
6/4/2017 20:16	61	8/4/2017 21:21	62	9/4/2017 14:26	61	10/4/2017 19:31	61	12/4/2017 20:36	64	14/4/2017 9:41	61
6/4/2017 20:21	61	8/4/2017 21:26	61	9/4/2017 14:31	61	10/4/2017 19:36	61	12/4/2017 20:41	62	14/4/2017 9:46	61
6/4/2017 20:26	62	8/4/2017 21:31	61	9/4/2017 14:36	61	10/4/2017 19:41	61	12/4/2017 20:46	63	14/4/2017 9:51	61
6/4/2017 20:31	61	8/4/2017 21:36	61	9/4/2017 14:41	61	10/4/2017 19:46	61	12/4/2017 20:51	62	14/4/2017 9:56	62
6/4/2017 20:36	61	8/4/2017 21:41	61	9/4/2017 14:46	61	10/4/2017 19:51	61	12/4/2017 20:56	62	14/4/2017 10:01	61
6/4/2017 20:41	61	8/4/2017 21:46	61	9/4/2017 14:51	62	10/4/2017 19:56	61	12/4/2017 21:01	61	14/4/2017 10:06	61
6/4/2017 20:46	61	8/4/2017 21:51	59	9/4/2017 14:56	61	10/4/2017 20:01	61	12/4/2017 21:06	61	14/4/2017 10:11	61
6/4/2017 20:51	61	8/4/2017 21:56	61	9/4/2017 15:01	61	10/4/2017 20:06	61	12/4/2017 21:11	61	14/4/2017 10:16	60
6/4/2017 20:56	62	8/4/2017 22:01	61	9/4/2017 15:06	60	10/4/2017 20:11	63	12/4/2017 21:16	61	14/4/2017 10:21	61
6/4/2017 21:01	61	8/4/2017 22:06	60	9/4/2017 15:11	61	10/4/2017 20:16	61	12/4/2017 21:21	62	14/4/2017 10:26	61
6/4/2017 21:06	61	8/4/2017 22:11	60	9/4/2017 15:16	61	10/4/2017 20:21	61	12/4/2017 21:26	62	14/4/2017 10:31	62
6/4/2017 21:11	62	8/4/2017 22:16	60	9/4/2017 15:21	61	10/4/2017 20:26	60	12/4/2017 21:31	61	14/4/2017 10:36	62
6/4/2017 21:16	62	8/4/2017 22:21	59	9/4/2017 15:26	61	10/4/2017 20:31	61	12/4/2017 21:36	62	14/4/2017 10:41	62
6/4/2017 21:21	61	8/4/2017 22:26	60	9/4/2017 15:31	61	10/4/2017 20:36	61	12/4/2017 21:41	61	14/4/2017 10:46	61
6/4/2017 21:26	61	8/4/2017 22:31	60	9/4/2017 15:36	61	10/4/2017 20:41	61	12/4/2017 21:46	61	14/4/2017 10:51	62
6/4/2017 21:31	63	8/4/2017 22:36	62	9/4/2017 15:41	61	10/4/2017 20:46	61	12/4/2017 21:51	61	14/4/2017 10:56	61
6/4/2017 21:36	61	8/4/2017 22:41	60	9/4/2017 15:46	61	10/4/2017 20:51	60	12/4/2017 21:56	61	14/4/2017 11:01	63
6/4/2017 21:41	62	8/4/2017 22:46	60	9/4/2017 15:51	61	10/4/2017 20:56	60	12/4/2017 22:01	61	14/4/2017 11:06	62
6/4/2017 21:46	61	8/4/2017 22:51	61	9/4/2017 15:56	62	10/4/2017 21:01	60	12/4/2017 22:06	62	14/4/2017 11:11	62
6/4/2017 21:51	61	8/4/2017 22:56	63	9/4/2017 16:01	61	10/4/2017 21:06	60	12/4/2017 22:11	62	14/4/2017 11:16	61
6/4/2017 21:56	60	9/4/2017 7:01	60	9/4/2017 16:06	61	10/4/2017 21:11	61	12/4/2017 22:16	62	14/4/2017 11:21	61
6/4/2017 22:01	60	9/4/2017 7:06	59	9/4/2017 16:11	62	10/4/2017 21:16	60	12/4/2017 22:21	61	14/4/2017 11:26	61
6/4/2017 22:06	61	9/4/2017 7:11	61	9/4/2017 16:16	61	10/4/2017 21:21	60	12/4/2017 22:26	61	14/4/2017 11:31	61
6/4/2017 22:11	61	9/4/2017 7:16	60	9/4/2017 16:21	61	10/4/2017 21:26	59	12/4/2017 22:31	61	14/4/2017 11:36	59
6/4/2017 22:16	61	9/4/2017 7:21	61	9/4/2017 16:26	62	10/4/2017 21:31	59	12/4/2017 22:36	61	14/4/2017 11:41	60
6/4/2017 22:21	60	9/4/2017 7:26	62	9/4/2017 16:31	62	10/4/2017 21:36	60	12/4/2017 22:41	62	14/4/2017 11:46	60
6/4/2017 22:26	61	9/4/2017 7:31	59	9/4/2017 16:36	61	10/4/2017 21:41	59	12/4/2017 22:46	60	14/4/2017 11:51	60
6/4/2017 22:31	60	9/4/2017 7:36	58	9/4/2017 16:41	62	10/4/2017 21:46	60	12/4/2017 22:51	61	14/4/2017 11:56	60
6/4/2017 22:36	60	9/4/2017 7:41	59	9/4/2017 16:46	62	10/4/2017 21:51	60	12/4/2017 22:56	61	14/4/2017 12:01	59
6/4/2017 22:41	60	9/4/2017 7:46	60	9/4/2017 16:51	62	10/4/2017 21:56	60	13/4/2017 19:01	60	14/4/2017 12:06	60
6/4/2017 22:46	60	9/4/2017 7:51	59	9/4/2017 16:56	61	10/4/2017 22:01	59	13/4/2017 19:06	59	14/4/2017 12:11	59
6/4/2017 22:51	60	9/4/2017 7:56	59	9/4/2017 17:01	61	10/4/2017 22:06	60	13/4/2017 19:11	60	14/4/2017 12:16	60
6/4/2017 22:56	60	9/4/2017 8:01	59	9/4/2017 17:06	61	10/4/2017 22:11	60	13/4/2017 19:16	60	14/4/2017 12:21	61
7/4/2017 19:01	63	9/4/2017 8:06	60	9/4/2017 17:11	61	10/4/2017 22:16	59	13/4/2017 19:21	60	14/4/2017 12:26	61
7/4/2017 19:06	61	9/4/2017 8:11	59	9/4/2017 17:16	61	10/4/2017 22:21	59	13/4/2017 19:26	60	14/4/2017 12:31	61
7/4/2017 19:11	61	9/4/2017 8:16	60	9/4/2017 17:21	61	10/4/2017 22:26	61	13/4/2017 19:31	61	14/4/2017 12:36	61
7/4/2017 19:16	54	9/4/2017 8:21	61	9/4/2017 17:26	61	10/4/2017 22:31	60	13/4/2017 19:36	61	14/4/2017 12:41	61
7/4/2017 19:21	61	9/4/2017 8:26	60	9/4/2017 17:31	61	10/4/2017 22:36	59	13/4/2017 19:41	63	14/4/2017 12:46	61
7/4/2017 19:26	62	9/4/2017 8:31	61	9/4/2017 17:36	61	10/4/2017 22:41	60	13/4/2017 19:46	61	14/4/2017 12:51	61
7/4/2017 19:31	61	9/4/2017 8:36	60	9/4/2017 17:41	62	10/4/2017 22:46	59	13/4/2017 19:51	62	14/4/2017 12:56	61
7/4/2017 19:36	60	9/4/2017 8:41	60	9/4/2017 17:46	62	10/4/2017 22:51	59	13/4/2017 19:56	61	14/4/2017 13:01	62
7/4/2017 19:41	61	9/4/2017 8:46	60	9/4/2017 17:51	62	10/4/2017 22:56	59	13/4/2017 20:01	62	14/4/2017 13:06	61
7/4/201											

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
14/4/2017 16:01	61	15/4/2017 9:06	61	15/4/2017 18:11	61	16/4/2017 11:16	60	16/4/2017 20:21	61	17/4/2017 13:26	61
14/4/2017 16:06	61	15/4/2017 9:11	62	15/4/2017 18:16	62	16/4/2017 11:21	62	16/4/2017 20:26	60	17/4/2017 13:31	61
14/4/2017 16:11	61	15/4/2017 9:16	61	15/4/2017 18:21	61	16/4/2017 11:26	61	16/4/2017 20:31	59	17/4/2017 13:36	62
14/4/2017 16:16	62	15/4/2017 9:21	61	15/4/2017 18:26	61	16/4/2017 11:31	61	16/4/2017 20:36	59	17/4/2017 13:41	61
14/4/2017 16:21	62	15/4/2017 9:26	61	15/4/2017 18:31	60	16/4/2017 11:36	62	16/4/2017 20:41	59	17/4/2017 13:46	62
14/4/2017 16:26	61	15/4/2017 9:31	61	15/4/2017 18:36	61	16/4/2017 11:41	61	16/4/2017 20:46	60	17/4/2017 13:51	61
14/4/2017 16:31	61	15/4/2017 9:36	64	15/4/2017 18:41	61	16/4/2017 11:46	62	16/4/2017 20:51	59	17/4/2017 13:56	62
14/4/2017 16:36	61	15/4/2017 9:41	61	15/4/2017 18:46	61	16/4/2017 11:51	61	16/4/2017 20:56	60	17/4/2017 14:01	61
14/4/2017 16:41	62	15/4/2017 9:46	62	15/4/2017 18:51	61	16/4/2017 11:56	61	16/4/2017 21:01	60	17/4/2017 14:06	61
14/4/2017 16:46	61	15/4/2017 9:51	61	15/4/2017 18:56	61	16/4/2017 12:01	60	16/4/2017 21:06	59	17/4/2017 14:11	63
14/4/2017 16:51	60	15/4/2017 9:56	62	15/4/2017 19:01	61	16/4/2017 12:06	61	16/4/2017 21:11	59	17/4/2017 14:16	61
14/4/2017 16:56	62	15/4/2017 10:01	61	15/4/2017 19:06	62	16/4/2017 12:11	62	16/4/2017 21:16	59	17/4/2017 14:21	59
14/4/2017 17:01	61	15/4/2017 10:06	61	15/4/2017 19:11	61	16/4/2017 12:16	61	16/4/2017 21:21	59	17/4/2017 14:26	59
14/4/2017 17:06	61	15/4/2017 10:11	61	15/4/2017 19:16	61	16/4/2017 12:21	63	16/4/2017 21:26	59	17/4/2017 14:31	57
14/4/2017 17:11	61	15/4/2017 10:16	62	15/4/2017 19:21	61	16/4/2017 12:26	61	16/4/2017 21:31	60	17/4/2017 14:36	61
14/4/2017 17:16	61	15/4/2017 10:21	61	15/4/2017 19:26	60	16/4/2017 12:31	61	16/4/2017 21:36	59	17/4/2017 14:41	62
14/4/2017 17:21	61	15/4/2017 10:26	61	15/4/2017 19:31	61	16/4/2017 12:36	62	16/4/2017 21:41	59	17/4/2017 14:46	61
14/4/2017 17:26	61	15/4/2017 10:31	61	15/4/2017 19:36	61	16/4/2017 12:41	63	16/4/2017 21:46	60	17/4/2017 14:51	62
14/4/2017 17:31	61	15/4/2017 10:36	61	15/4/2017 19:41	60	16/4/2017 12:46	61	16/4/2017 21:51	59	17/4/2017 14:56	61
14/4/2017 17:36	61	15/4/2017 10:41	61	15/4/2017 19:46	61	16/4/2017 12:51	61	16/4/2017 21:56	59	17/4/2017 15:01	62
14/4/2017 17:41	61	15/4/2017 10:46	61	15/4/2017 19:51	61	16/4/2017 12:56	61	16/4/2017 22:01	60	17/4/2017 15:06	61
14/4/2017 17:46	61	15/4/2017 10:51	60	15/4/2017 19:56	60	16/4/2017 13:01	62	16/4/2017 22:06	60	17/4/2017 15:11	61
14/4/2017 17:51	61	15/4/2017 10:56	62	15/4/2017 20:01	61	16/4/2017 13:06	61	16/4/2017 22:11	59	17/4/2017 15:16	59
14/4/2017 17:56	61	15/4/2017 11:01	60	15/4/2017 20:06	62	16/4/2017 13:11	61	16/4/2017 22:16	59	17/4/2017 15:21	60
14/4/2017 18:01	61	15/4/2017 11:06	60	15/4/2017 20:11	61	16/4/2017 13:16	62	16/4/2017 22:21	60	17/4/2017 15:26	57
14/4/2017 18:06	61	15/4/2017 11:11	61	15/4/2017 20:16	61	16/4/2017 13:21	62	16/4/2017 22:26	60	17/4/2017 15:31	61
14/4/2017 18:11	61	15/4/2017 11:16	61	15/4/2017 20:21	59	16/4/2017 13:26	61	16/4/2017 22:31	60	17/4/2017 15:36	62
14/4/2017 18:16	61	15/4/2017 11:21	62	15/4/2017 20:26	60	16/4/2017 13:31	62	16/4/2017 22:36	59	17/4/2017 15:41	62
14/4/2017 18:21	61	15/4/2017 11:26	63	15/4/2017 20:31	60	16/4/2017 13:36	62	16/4/2017 22:41	60	17/4/2017 15:46	61
14/4/2017 18:26	62	15/4/2017 11:31	61	15/4/2017 20:36	60	16/4/2017 13:41	61	16/4/2017 22:46	59	17/4/2017 15:51	62
14/4/2017 18:31	61	15/4/2017 11:36	61	15/4/2017 20:41	60	16/4/2017 13:46	62	16/4/2017 22:51	58	17/4/2017 15:56	63
14/4/2017 18:36	61	15/4/2017 11:41	62	15/4/2017 20:46	61	16/4/2017 13:51	61	16/4/2017 22:56	59	17/4/2017 16:01	62
14/4/2017 18:41	61	15/4/2017 11:46	62	15/4/2017 20:51	60	16/4/2017 13:56	62	17/4/2017 7:01	60	17/4/2017 16:06	57
14/4/2017 18:46	61	15/4/2017 11:51	61	15/4/2017 20:56	60	16/4/2017 14:01	62	17/4/2017 7:06	59	17/4/2017 16:11	61
14/4/2017 18:51	62	15/4/2017 11:56	61	15/4/2017 21:01	59	16/4/2017 14:06	60	17/4/2017 7:11	61	17/4/2017 16:16	62
14/4/2017 18:56	61	15/4/2017 12:01	62	15/4/2017 21:06	60	16/4/2017 14:11	61	17/4/2017 7:16	59	17/4/2017 16:21	63
14/4/2017 19:01	62	15/4/2017 12:06	62	15/4/2017 21:11	59	16/4/2017 14:16	61	17/4/2017 7:21	58	17/4/2017 16:26	64
14/4/2017 19:06	61	15/4/2017 12:11	61	15/4/2017 21:16	60	16/4/2017 14:21	61	17/4/2017 7:26	59	17/4/2017 16:31	62
14/4/2017 19:11	61	15/4/2017 12:16	61	15/4/2017 21:21	63	16/4/2017 14:26	62	17/4/2017 7:31	60	17/4/2017 16:36	63
14/4/2017 19:16	61	15/4/2017 12:21	61	15/4/2017 21:26	61	16/4/2017 14:31	61	17/4/2017 7:36	59	17/4/2017 16:41	62
14/4/2017 19:21	60	15/4/2017 12:26	61	15/4/2017 21:31	60	16/4/2017 14:36	61	17/4/2017 7:41	59	17/4/2017 16:46	62
14/4/2017 19:26	61	15/4/2017 12:31	61	15/4/2017 21:36	61	16/4/2017 14:41	61	17/4/2017 7:46	61	17/4/2017 16:51	64
14/4/2017 19:31	62	15/4/2017 12:36	61	15/4/2017 21:41	60	16/4/2017 14:46	60	17/4/2017 7:51	60	17/4/2017 16:56	62
14/4/2017 19:36	62	15/4/2017 12:41	63	15/4/2017 21:46	59	16/4/2017 14:51	61	17/4/2017 7:56	59	17/4/2017 17:01	60
14/4/2017 19:41	61	15/4/2017 12:46	61	15/4/2017 21:51	60	16/4/2017 14:56	61	17/4/2017 8:01	59	17/4/2017 17:06	59
14/4/2017 19:46	61	15/4/2017 12:51	61	15/4/2017 21:56	60	16/4/2017 15:01	62	17/4/2017 8:06	60	17/4/2017 17:11	59
14/4/2017 19:51	60	15/4/2017 12:56	62	15/4/2017 22:01	60	16/4/2017 15:06	61	17/4/2017 8:11	59	17/4/2017 17:16	62
14/4/2017 19:56	61	15/4/2017 13:01	62	15/4/2017 22:06	59	16/4/2017 15:11	60	17/4/2017 8:16	60	17/4/2017 17:21	62
14/4/2017 20:01	60	15/4/2017 13:06	61	15/4/2017 22:11	60	16/4/2017 15:16	61	17/4/2017 8:21	59	17/4/2017 17:26	62
14/4/2017 20:06	61	15/4/2017 13:11	61	15/4/2017 22:16	59	16/4/2017 15:21	59	17/4/2017 8:26	59	17/4/2017 17:31	62
14/4/2017 20:11	60	15/4/2017 13:16	61	15/4/2017 22:21	59	16/4/2017 15:26	61	17/4/2017 8:31	60	17/4/2017 17:36	62
14/4/2017 20:16	60	15/4/2017 13:21	62	15/4/2017 22:26	59	16/4/2017 15:31	61	17/4/2017 8:36	62	17/4/2017 17:41	61
14/4/2017 20:21	60	15/4/2017 13:26	61	15/4/2017 22:31	62	16/4/2017 15:36	60	17/4/2017 8:41	61	17/4/2017 17:46	61
14/4/2017 20:26	61	15/4/2017 13:31	62	15/4/2017 22:36	59	16/4/2017 15:41	61	17/4/2017 8:46	60	17/4/2017 17:51	61
14/4/2017 20:31	62	15/4/2017 13:36	62	15/4/2017 22:41	60	16/4/2017 15:46	61	17/4/2017 8:51	60	17/4/2017 17:56	62
14/4/2017 20:36	61	15/4/2017 13:41	62	15/4/2017 22:46	60	16/4/2017 15:51	61	17/4/2017 8:56	60	17/4/2017 18:01	61
14/4/2017 20:41	61	15/4/2017 13:46	61	15/4/2017 22:51	60	16/4/2017 15:56	62	17/4/2017 9:01	61	17/4/2017 18:06	61
14/4/2017 20:46	60	15/4/2017 13:51	62	15/4/2017 22:56	60	16/4/2017 16:01	61	17/4/2017 9:06	60	17/4/2017 18:11	61
14/4/2017 20:51	61	15/4/2017 13:56	62	16/4/2017 7:01	62	16/4/2017 16:06	60	17/4/2017 9:11	60	17/4/2017 18:16	62
14/4/2017 20:56	62	15/4/2017 14:01	61	16/4/2017 7:06	59	16/4/2017 16:11	63	17/4/2017 9:16	60	17/4/2017 18:21	61
14/4/2017 21:01	60	15/4/2017 14:06	61	16/4/2017 7:11	57	16/4/2017 16:16	60	17/4/2017 9:21	60	17/4/2017 18:26	61
14/4/2017 21:06	60	15/4/2017 14:11	61	16/4/2017 7:16	57	16/4/2017 16:21	61	17/4/2017 9:26	62	17/4/2017 18:31	61
14/4/2017 21:11	61	15/4/2017 14:16	61	16/4/2017 7:21	60	16/4/2017 16:26	61	17/4/2017 9:31	61	17/4/2017 18:36	61
14/4/2017 21:16	62	15/4/2017 14:21	61	16/4/2017 7:26	59	16/4/2017 16:31	60	17/4/2017 9:36	61	17/4/2017 18:41	61
14/4/2017 21:21	61	15/4/2017 14:26	61	16/4/2017 7:31	59	16/4/2017 16:36	60	17/4/2017 9:41	60	17/4/2017 18:46	61
14/4/2017 21:26	63	15/4/2017 14:31	61	16/4/2017 7:36	59	16/4/2017 16:41	60	17/4/2017 9:46	60	17/4/2017 18:51	60
14/4/2017 21:31	63	15/4/2017 14:36	62	16/4/2017 7:41	59	16/4/2017 16:46	60	17/4/2017 9:51	60	17/4/2017 18:56	62
14/4/2017 21:36	42	15/4/2017 14:41	62	16/4/2017 7:46	59	16/4/2017 16:51	60	17/4/2017 9:56	60	17/4/2017 19:01	61
14/4/2017 21:41	60	15/4/2017 14:46	61	16/4/2017 7:51	58	16/4/2017 16:56	60	17/4/2017 10:01	60	17/4/2017 19:06	61
14/4/2017 21:46	60	15/4/2017 14:51	61	16/4/2017 7:56	58	16/4/2017 17:01	61	17/4/2017 10:06	60	17/4/2017 19:11	62
14/4/2017 21:51	60	15/4/2017 14:56	61	16/4/2017 8:01	59	16/4/2017 17:06	61	17/4/2017 10:11	60	17/4/2017 19:16	62
14/4/2017 21:56	63	15/4/2017 15:01	61	16/4/2017 8:06	59	16/4/2017 17:11	61	17/4/2017 10:16	61	17/4/2017 19:21	61
14/4/2017 22:01	60	15/4/2017 15:06	61	16/4/2017 8:11	59	16/4/2017 17:16	60	17/4/2017 10:21	61	17/4/2017 19:26	61
14/4/2017 22:06	62	15/4/2017 15:11	61	16/4/2017 8:16							

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)											
17/4/2017 22:31	59	20/4/2017 19:36	61	22/4/2017 20:41	61	23/4/2017 13:46	61	23/4/2017 22:51	59	26/4/2017 19:56	62		
17/4/2017 22:36	59	20/4/2017 19:41	62	22/4/2017 20:46	61	23/4/2017 13:51	63	23/4/2017 22:56	58	26/4/2017 20:01	61		
17/4/2017 22:41	58	20/4/2017 19:46	61	22/4/2017 20:51	60	23/4/2017 13:56	61	24/4/2017 19:01	61	26/4/2017 20:06	62		
17/4/2017 22:46	59	20/4/2017 19:51	61	22/4/2017 20:56	61	23/4/2017 14:01	60	24/4/2017 19:06	62	26/4/2017 20:11	62		
17/4/2017 22:51	59	20/4/2017 19:56	61	22/4/2017 21:01	60	23/4/2017 14:06	62	24/4/2017 19:11	61	26/4/2017 20:16	62		
17/4/2017 22:56	58	20/4/2017 20:01	61	22/4/2017 21:06	61	23/4/2017 14:11	61	24/4/2017 19:16	62	26/4/2017 20:21	62		
18/4/2017 19:01	62	20/4/2017 20:06	61	22/4/2017 21:11	62	23/4/2017 14:16	62	24/4/2017 19:21	62	26/4/2017 20:26	61		
18/4/2017 19:06	62	20/4/2017 20:11	61	22/4/2017 21:16	60	23/4/2017 14:21	62	24/4/2017 19:26	63	26/4/2017 20:31	62		
18/4/2017 19:11	62	20/4/2017 20:16	61	22/4/2017 21:21	61	23/4/2017 14:26	62	24/4/2017 19:31	62	26/4/2017 20:36	63		
18/4/2017 19:16	62	20/4/2017 20:21	60	22/4/2017 21:26	61	23/4/2017 14:31	62	24/4/2017 19:36	62	26/4/2017 20:41	61		
18/4/2017 19:21	62	20/4/2017 20:26	60	22/4/2017 21:31	60	23/4/2017 14:36	62	24/4/2017 19:41	63	26/4/2017 20:46	61		
18/4/2017 19:26	62	20/4/2017 20:31	60	22/4/2017 21:36	62	23/4/2017 14:41	62	24/4/2017 19:46	62	26/4/2017 20:51	61		
18/4/2017 19:31	62	20/4/2017 20:36	60	22/4/2017 21:41	61	23/4/2017 14:46	63	24/4/2017 19:51	63	26/4/2017 20:56	61		
18/4/2017 19:36	62	20/4/2017 20:41	61	22/4/2017 21:46	61	23/4/2017 14:51	61	24/4/2017 19:56	62	26/4/2017 21:01	62		
18/4/2017 19:41	62	20/4/2017 20:46	61	22/4/2017 21:51	61	23/4/2017 14:56	62	24/4/2017 20:01	62	26/4/2017 21:06	61		
18/4/2017 19:46	62	20/4/2017 20:51	60	22/4/2017 21:56	60	23/4/2017 15:01	61	24/4/2017 20:06	62	26/4/2017 21:11	63		
18/4/2017 19:51	62	20/4/2017 20:56	61	22/4/2017 22:01	59	23/4/2017 15:06	62	24/4/2017 20:11	63	26/4/2017 21:16	62		
18/4/2017 19:56	62	20/4/2017 21:01	60	22/4/2017 22:06	63	23/4/2017 15:11	61	24/4/2017 20:16	62	26/4/2017 21:21	61		
18/4/2017 20:01	62	20/4/2017 21:06	60	22/4/2017 22:11	61	23/4/2017 15:16	62	24/4/2017 20:21	63	26/4/2017 21:26	61		
18/4/2017 20:06	62	20/4/2017 21:11	60	22/4/2017 22:16	62	23/4/2017 15:21	62	24/4/2017 20:26	62	26/4/2017 21:31	60		
18/4/2017 20:11	62	20/4/2017 21:16	60	22/4/2017 22:21	60	23/4/2017 15:26	62	24/4/2017 20:31	62	26/4/2017 21:36	61		
18/4/2017 20:16	62	20/4/2017 21:21	61	22/4/2017 22:26	61	23/4/2017 15:31	63	24/4/2017 20:36	62	26/4/2017 21:41	63		
18/4/2017 20:21	62	20/4/2017 21:26	60	22/4/2017 22:31	60	23/4/2017 15:36	62	24/4/2017 20:41	62	26/4/2017 21:46	60		
18/4/2017 20:26	61	20/4/2017 21:31	60	22/4/2017 22:36	60	23/4/2017 15:41	61	24/4/2017 20:46	61	26/4/2017 21:51	60		
18/4/2017 20:31	62	20/4/2017 21:36	60	22/4/2017 22:41	60	23/4/2017 15:46	62	24/4/2017 20:51	62	26/4/2017 21:56	61		
18/4/2017 20:36	62	20/4/2017 21:41	60	22/4/2017 22:46	59	23/4/2017 15:51	61	24/4/2017 20:56	62	26/4/2017 22:01	61		
18/4/2017 20:41	62	20/4/2017 21:46	60	22/4/2017 22:51	59	23/4/2017 15:56	60	24/4/2017 21:01	62	26/4/2017 22:06	61		
18/4/2017 20:46	62	20/4/2017 21:51	60	22/4/2017 22:56	61	23/4/2017 16:01	61	24/4/2017 21:06	62	26/4/2017 22:11	63		
18/4/2017 20:51	62	20/4/2017 21:56	59	23/4/2017 7:01	61	23/4/2017 16:06	60	24/4/2017 21:11	61	26/4/2017 22:16	60		
18/4/2017 20:56	62	20/4/2017 22:01	60	23/4/2017 7:06	59	23/4/2017 16:11	60	24/4/2017 21:16	61	26/4/2017 22:21	60		
18/4/2017 21:01	62	20/4/2017 22:06	59	23/4/2017 7:11	60	23/4/2017 16:16	61	24/4/2017 21:21	63	26/4/2017 22:26	60		
18/4/2017 21:06	61	20/4/2017 22:11	60	23/4/2017 7:16	59	23/4/2017 16:21	61	24/4/2017 21:26	62	26/4/2017 22:31	61		
18/4/2017 21:11	62	20/4/2017 22:16	59	23/4/2017 7:21	61	23/4/2017 16:26	59	24/4/2017 21:31	61	26/4/2017 22:36	60		
18/4/2017 21:16	62	20/4/2017 22:21	60	23/4/2017 7:26	59	23/4/2017 16:31	63	24/4/2017 21:36	61	26/4/2017 22:41	60		
18/4/2017 21:21	62	20/4/2017 22:26	60	23/4/2017 7:31	59	23/4/2017 16:36	62	24/4/2017 21:41	63	26/4/2017 22:46	59		
18/4/2017 21:26	62	20/4/2017 22:31	60	23/4/2017 7:36	59	23/4/2017 16:41	62	24/4/2017 21:46	61	26/4/2017 22:51	60		
18/4/2017 21:31	62	20/4/2017 22:36	60	23/4/2017 7:41	59	23/4/2017 16:46	62	24/4/2017 21:51	62	26/4/2017 22:56	59		
18/4/2017 21:36	61	20/4/2017 22:41	60	23/4/2017 7:46	60	23/4/2017 16:51	62	24/4/2017 21:56	62				
18/4/2017 21:41	61	20/4/2017 22:46	59	23/4/2017 7:51	60	23/4/2017 16:56	62	24/4/2017 22:01	61	Night time: 23:00-07:00			
18/4/2017 21:46	61	20/4/2017 22:51	59	23/4/2017 7:56	59	23/4/2017 17:01	62	24/4/2017 22:06	61				
18/4/2017 21:51	61	20/4/2017 22:56	59	23/4/2017 8:01	61	23/4/2017 17:06	62	24/4/2017 22:11	61	27/3/2017 0:01	57		
18/4/2017 21:56	62	21/4/2017 19:01	59	23/4/2017 8:06	60	23/4/2017 17:11	62	24/4/2017 22:16	61	27/3/2017 0:06	57		
18/4/2017 22:01	61	21/4/2017 19:06	63	23/4/2017 8:11	59	23/4/2017 17:16	62	24/4/2017 22:21	61	27/3/2017 0:11	57		
18/4/2017 22:06	61	21/4/2017 19:11	61	23/4/2017 8:16	60	23/4/2017 17:21	61	24/4/2017 22:26	61	27/3/2017 0:16	58		
18/4/2017 22:11	60	21/4/2017 19:16	63	23/4/2017 8:21	61	23/4/2017 17:26	62	24/4/2017 22:31	61	27/3/2017 0:21	56		
18/4/2017 22:16	61	21/4/2017 19:21	61	23/4/2017 8:26	60	23/4/2017 17:31	62	24/4/2017 22:36	61	27/3/2017 0:26	57		
18/4/2017 22:21	61	21/4/2017 19:26	61	23/4/2017 8:31	61	23/4/2017 17:36	63	24/4/2017 22:41	61	27/3/2017 0:31	59		
18/4/2017 22:26	62	21/4/2017 19:31	61	23/4/2017 8:36	62	23/4/2017 17:41	61	24/4/2017 22:46	60	27/3/2017 0:36	56		
18/4/2017 22:31	60	21/4/2017 19:36	60	23/4/2017 8:41	60	23/4/2017 17:46	61	24/4/2017 22:51	61	27/3/2017 0:41	57		
18/4/2017 22:36	60	21/4/2017 19:41	62	23/4/2017 8:46	61	23/4/2017 17:51	61	24/4/2017 22:56	60	27/3/2017 0:46	56		
18/4/2017 22:41	61	21/4/2017 19:46	62	23/4/2017 8:51	61	23/4/2017 17:56	62	25/4/2017 19:01	61	27/3/2017 0:51	56		
18/4/2017 22:46	61	21/4/2017 19:51	62	23/4/2017 8:56	61	23/4/2017 18:01	62	25/4/2017 19:06	60	27/3/2017 0:56	57		
18/4/2017 22:51	61	21/4/2017 19:56	62	23/4/2017 9:01	60	23/4/2017 18:06	61	25/4/2017 19:11	60	27/3/2017 1:01	57		
18/4/2017 22:56	61	21/4/2017 20:01	61	23/4/2017 9:06	62	23/4/2017 18:11	61	25/4/2017 19:16	61	27/3/2017 1:06	56		
19/4/2017 19:01	61	21/4/2017 20:06	61	23/4/2017 9:11	61	23/4/2017 18:16	61	25/4/2017 19:21	60	27/3/2017 1:11	56		
19/4/2017 19:06	61	21/4/2017 20:11	61	23/4/2017 9:16	61	23/4/2017 18:21	62	25/4/2017 19:26	60	27/3/2017 1:16	57		
19/4/2017 19:11	61	21/4/2017 20:16	62	23/4/2017 9:21	62	23/4/2017 18:26	61	25/4/2017 19:31	60	27/3/2017 1:21	57		
19/4/2017 19:16	61	21/4/2017 20:21	62	23/4/2017 9:26	61	23/4/2017 18:31	60	25/4/2017 19:36	61	27/3/2017 1:26	55		
19/4/2017 19:21	61	21/4/2017 20:26	62	23/4/2017 9:31	61	23/4/2017 18:36	59	25/4/2017 19:41	61	27/3/2017 1:31	56		
19/4/2017 19:26	62	21/4/2017 20:31	62	23/4/2017 9:36	61	23/4/2017 18:41	60	25/4/2017 19:46	60	27/3/2017 1:36	55		
19/4/2017 19:31	61	21/4/2017 20:36	62	23/4/2017 9:41	62	23/4/2017 18:46	60	25/4/2017 19:51	60	27/3/2017 1:41	56		
19/4/2017 19:36	61	21/4/2017 20:41	61	23/4/2017 9:46	61	23/4/2017 18:51	61	25/4/2017 19:56	61	27/3/2017 1:46	54		
19/4/2017 19:41	61	21/4/2017 20:46	61	23/4/2017 9:51	61	23/4/2017 18:56	60	25/4/2017 20:01	62	27/3/2017 1:51	55		
19/4/2017 19:46	61	21/4/2017 20:51	60	23/4/2017 9:56	62	23/4/2017 19:01	61	25/4/2017 20:06	61	27/3/2017 1:56	55		
19/4/2017 19:51	61	21/4/2017 20:56	61	23/4/2017 10:01	61	23/4/2017 19:06	64	25/4/2017 20:11	63	27/3/2017 2:01	54		
19/4/2017 19:56	61	21/4/2017 21:01	61	23/4/2017 10:06	61	23/4/2017 19:11	61	25/4/2017 20:16	62	27/3/2017 2:06	55		
19/4/2017 20:01	61	21/4/2017 21:06	61	23/4/2017 10:11	61	23/4/2017 19:16	61	25/4/2017 20:21	61	27/3/2017 2:11	55		
19/4/2017 20:06	61	21/4/2017 21:11	60	23/4/2017 10:16	61	23/4/2017 19:21	60	25/4/2017 20:26	61	27/3/2017 2:16	54		
19/4/2017 20:11	61	21/4/2017 21:16	60	23/4/2017 10:21	62	23/4/2017 19:26	61	25/4/2017 20:31	62	27/3/2017 2:21	55		
19/4/2017 20:16	61	21/4/2017 21:21	62	23/4/2017 10:26	62	23/4/2017 19:31	61	25/4/2017 20:36	61	27/3/2017 2:26	54		
19/4/2017 20:21</													

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)											
27/3/2017 5:46	57	28/3/2017 6:51	50	29/3/2017 23:56	58	31/3/2017 1:01	57	1/4/2017 2:06	60	2/4/2017 3:11	57		
27/3/2017 5:51	58	28/3/2017 6:56	60	30/3/2017 0:01	58	31/3/2017 1:06	57	1/4/2017 2:11	59	2/4/2017 3:16	56		
27/3/2017 5:56	57	28/3/2017 23:01	60	30/3/2017 0:06	58	31/3/2017 1:11	57	1/4/2017 2:16	59	2/4/2017 3:21	56		
27/3/2017 6:01	56	28/3/2017 23:06	59	30/3/2017 0:11	57	31/3/2017 1:16	57	1/4/2017 2:21	60	2/4/2017 3:26	56		
27/3/2017 6:06	58	28/3/2017 23:11	59	30/3/2017 0:16	58	31/3/2017 1:21	56	1/4/2017 2:26	59	2/4/2017 3:31	56		
27/3/2017 6:11	58	28/3/2017 23:16	58	30/3/2017 0:21	58	31/3/2017 1:26	57	1/4/2017 2:31	59	2/4/2017 3:36	55		
27/3/2017 6:16	59	28/3/2017 23:21	59	30/3/2017 0:26	58	31/3/2017 1:31	56	1/4/2017 2:36	60	2/4/2017 3:41	55		
27/3/2017 6:21	59	28/3/2017 23:26	59	30/3/2017 0:31	58	31/3/2017 1:36	56	1/4/2017 2:41	59	2/4/2017 3:46	56		
27/3/2017 6:26	60	28/3/2017 23:31	59	30/3/2017 0:36	59	31/3/2017 1:41	55	1/4/2017 2:46	59	2/4/2017 3:51	57		
27/3/2017 6:31	60	28/3/2017 23:36	58	30/3/2017 0:41	59	31/3/2017 1:46	57	1/4/2017 2:51	59	2/4/2017 3:56	55		
27/3/2017 6:36	45	28/3/2017 23:41	58	30/3/2017 0:46	57	31/3/2017 1:51	57	1/4/2017 2:56	59	2/4/2017 4:01	57		
27/3/2017 6:41	52	28/3/2017 23:46	59	30/3/2017 0:51	57	31/3/2017 1:56	57	1/4/2017 3:01	59	2/4/2017 4:06	54		
27/3/2017 6:46	54	28/3/2017 23:51	58	30/3/2017 0:56	57	31/3/2017 2:01	55	1/4/2017 3:06	59	2/4/2017 4:11	56		
27/3/2017 6:51	60	28/3/2017 23:56	58	30/3/2017 1:01	57	31/3/2017 2:06	55	1/4/2017 3:11	59	2/4/2017 4:16	55		
27/3/2017 6:56	60	29/3/2017 0:01	57	30/3/2017 1:06	57	31/3/2017 2:11	56	1/4/2017 3:16	59	2/4/2017 4:21	56		
27/3/2017 23:01	43	29/3/2017 0:06	58	30/3/2017 1:11	58	31/3/2017 2:16	57	1/4/2017 3:21	58	2/4/2017 4:26	55		
27/3/2017 23:06	59	29/3/2017 0:11	58	30/3/2017 1:16	57	31/3/2017 2:21	56	1/4/2017 3:26	59	2/4/2017 4:31	55		
27/3/2017 23:11	59	29/3/2017 0:16	58	30/3/2017 1:21	57	31/3/2017 2:26	55	1/4/2017 3:31	60	2/4/2017 4:36	55		
27/3/2017 23:16	59	29/3/2017 0:21	58	30/3/2017 1:26	56	31/3/2017 2:31	56	1/4/2017 3:36	59	2/4/2017 4:41	55		
27/3/2017 23:21	59	29/3/2017 0:26	58	30/3/2017 1:31	56	31/3/2017 2:36	54	1/4/2017 3:41	59	2/4/2017 4:46	55		
27/3/2017 23:26	59	29/3/2017 0:31	58	30/3/2017 1:36	56	31/3/2017 2:41	54	1/4/2017 3:46	59	2/4/2017 4:51	55		
27/3/2017 23:31	58	29/3/2017 0:36	56	30/3/2017 1:41	56	31/3/2017 2:46	55	1/4/2017 3:51	59	2/4/2017 4:56	55		
27/3/2017 23:36	57	29/3/2017 0:41	57	30/3/2017 1:46	57	31/3/2017 2:51	55	1/4/2017 3:56	59	2/4/2017 5:01	55		
27/3/2017 23:41	57	29/3/2017 0:46	56	30/3/2017 1:51	56	31/3/2017 2:56	57	1/4/2017 4:01	59	2/4/2017 5:06	56		
27/3/2017 23:46	57	29/3/2017 0:51	56	30/3/2017 1:56	56	31/3/2017 3:01	53	1/4/2017 4:06	59	2/4/2017 5:11	55		
27/3/2017 23:51	57	29/3/2017 0:56	56	30/3/2017 2:01	57	31/3/2017 3:06	55	1/4/2017 4:11	58	2/4/2017 5:16	55		
27/3/2017 23:56	57	29/3/2017 1:01	57	30/3/2017 2:06	55	31/3/2017 3:11	54	1/4/2017 4:16	59	2/4/2017 5:21	56		
28/3/2017 0:01	57	29/3/2017 1:06	56	30/3/2017 2:11	56	31/3/2017 3:16	55	1/4/2017 4:21	59	2/4/2017 5:26	56		
28/3/2017 0:06	56	29/3/2017 1:11	56	30/3/2017 2:16	55	31/3/2017 3:21	55	1/4/2017 4:26	59	2/4/2017 5:31	56		
28/3/2017 0:11	57	29/3/2017 1:16	56	30/3/2017 2:21	54	31/3/2017 3:26	55	1/4/2017 4:31	59	2/4/2017 5:36	56		
28/3/2017 0:16	58	29/3/2017 1:21	56	30/3/2017 2:26	55	31/3/2017 3:31	55	1/4/2017 4:36	58	2/4/2017 5:41	56		
28/3/2017 0:21	57	29/3/2017 1:26	58	30/3/2017 2:31	55	31/3/2017 3:36	54	1/4/2017 4:41	59	2/4/2017 5:46	56		
28/3/2017 0:26	56	29/3/2017 1:31	55	30/3/2017 2:36	56	31/3/2017 3:41	54	1/4/2017 4:46	59	2/4/2017 5:51	58		
28/3/2017 0:31	56	29/3/2017 1:36	55	30/3/2017 2:41	55	31/3/2017 3:46	54	1/4/2017 4:51	58	2/4/2017 5:56	57		
28/3/2017 0:36	56	29/3/2017 1:41	56	30/3/2017 2:46	56	31/3/2017 3:51	55	1/4/2017 4:56	59	2/4/2017 6:01	56		
28/3/2017 0:41	57	29/3/2017 1:46	56	30/3/2017 2:51	55	31/3/2017 3:56	54	1/4/2017 5:01	58	2/4/2017 6:06	57		
28/3/2017 0:46	56	29/3/2017 1:51	55	30/3/2017 2:56	55	31/3/2017 4:01	54	1/4/2017 5:06	59	2/4/2017 6:11	59		
28/3/2017 0:51	56	29/3/2017 1:56	55	30/3/2017 3:01	54	31/3/2017 4:06	54	1/4/2017 5:11	59	2/4/2017 6:16	59		
28/3/2017 0:56	57	29/3/2017 2:01	55	30/3/2017 3:06	54	31/3/2017 4:11	55	1/4/2017 5:16	58	2/4/2017 6:21	60		
28/3/2017 1:01	56	29/3/2017 2:06	55	30/3/2017 3:11	55	31/3/2017 4:16	55	1/4/2017 5:21	59	2/4/2017 6:26	60		
28/3/2017 1:06	57	29/3/2017 2:11	55	30/3/2017 3:16	54	31/3/2017 4:21	55	1/4/2017 5:26	59	2/4/2017 6:31	60		
28/3/2017 1:11	56	29/3/2017 2:16	55	30/3/2017 3:21	54	31/3/2017 4:26	55	1/4/2017 5:31	60	2/4/2017 6:36	59		
28/3/2017 1:16	56	29/3/2017 2:21	56	30/3/2017 3:26	55	31/3/2017 4:31	54	1/4/2017 5:36	59	2/4/2017 6:41	59		
28/3/2017 1:21	55	29/3/2017 2:26	55	30/3/2017 3:31	55	31/3/2017 4:36	55	1/4/2017 5:41	59	2/4/2017 6:46	59		
28/3/2017 1:26	55	29/3/2017 2:31	55	30/3/2017 3:36	55	31/3/2017 4:41	54	1/4/2017 5:46	59	2/4/2017 6:51	60		
28/3/2017 1:31	56	29/3/2017 2:36	55	30/3/2017 3:41	54	31/3/2017 4:46	54	1/4/2017 5:51	59	2/4/2017 6:56	59		
28/3/2017 1:36	56	29/3/2017 2:41	55	30/3/2017 3:46	56	31/3/2017 4:51	55	1/4/2017 5:56	60	2/4/2017 7:01	58		
28/3/2017 1:41	56	29/3/2017 2:46	55	30/3/2017 3:51	55	31/3/2017 4:56	55	1/4/2017 6:01	60	2/4/2017 7:06	59		
28/3/2017 1:46	55	29/3/2017 2:51	54	30/3/2017 3:56	54	31/3/2017 5:01	54	1/4/2017 6:06	60	2/4/2017 7:11	58		
28/3/2017 1:51	56	29/3/2017 2:56	55	30/3/2017 4:01	54	31/3/2017 5:06	55	1/4/2017 6:11	60	2/4/2017 7:16	59		
28/3/2017 1:56	55	29/3/2017 3:01	53	30/3/2017 4:06	55	31/3/2017 5:11	55	1/4/2017 6:16	61	2/4/2017 7:21	58		
28/3/2017 2:01	56	29/3/2017 3:06	54	30/3/2017 4:11	54	31/3/2017 5:16	55	1/4/2017 6:21	62	2/4/2017 7:26	58		
28/3/2017 2:06	56	29/3/2017 3:11	54	30/3/2017 4:16	55	31/3/2017 5:21	56	1/4/2017 6:26	61	2/4/2017 7:31	57		
28/3/2017 2:11	55	29/3/2017 3:16	53	30/3/2017 4:21	55	31/3/2017 5:26	55	1/4/2017 6:31	49	2/4/2017 7:36	59		
28/3/2017 2:16	54	29/3/2017 3:21	54	30/3/2017 4:26	55	31/3/2017 5:31	55	1/4/2017 6:36	52	2/4/2017 7:41	58		
28/3/2017 2:21	55	29/3/2017 3:26	55	30/3/2017 4:31	54	31/3/2017 5:36	56	1/4/2017 6:41	47	2/4/2017 7:46	57		
28/3/2017 2:26	53	29/3/2017 3:31	55	30/3/2017 4:36	55	31/3/2017 5:41	56	1/4/2017 6:46	48	2/4/2017 7:51	58		
28/3/2017 2:31	54	29/3/2017 3:36	55	30/3/2017 4:41	54	31/3/2017 5:46	56	1/4/2017 6:51	54	2/4/2017 7:56	57		
28/3/2017 2:36	55	29/3/2017 3:41	55	30/3/2017 4:46	54	31/3/2017 5:51	56	1/4/2017 6:56	49	3/4/2017 0:01	57		
28/3/2017 2:41	54	29/3/2017 3:46	55	30/3/2017 4:51	55	31/3/2017 5:56	57	1/4/2017 7:01	59	3/4/2017 0:06	57		
28/3/2017 2:46	55	29/3/2017 3:51	55	30/3/2017 4:56	54	31/3/2017 6:01	57	1/4/2017 7:06	60	3/4/2017 0:11	58		
28/3/2017 2:51	56	29/3/2017 3:56	54	30/3/2017 5:01	55	31/3/2017 6:06	59	1/4/2017 7:11	59	3/4/2017 0:16	57		
28/3/2017 2:56	54	29/3/2017 4:01	55	30/3/2017 5:06	54	31/3/2017 6:11	58	1/4/2017 7:16	59	3/4/2017 0:21	58		
28/3/2017 3:01	54	29/3/2017 4:06	56	30/3/2017 5:11	54	31/3/2017 6:16	59	1/4/2017 7:21	60	3/4/2017 0:26	56		
28/3/2017 3:06	54	29/3/2017 4:11	56	30/3/2017 5:16	55	31/3/2017 6:21	60	1/4/2017 7:26	60	3/4/2017 0:31	57		
28/3/2017 3:11	55	29/3/2017 4:16	54	30/3/2017 5:21	56	31/3/2017 6:26	60	1/4/2017 7:31	59	3/4/2017 0:36	57		
28/3/2017 3:16	54	29/3/2017 4:21	55	30/3/2017 5:26	56	31/3/2017 6:31	59	1/4/2017 7:36	59	3/4/2017 0:41	57		
28/3/2017 3:21	56	29/3/2017 4:26	56	30/3/2017 5:31	56	31/3/2017 6:36	61	1/4/2017 7:41	59	3/4/2017 0:46	56		
28/3/2017 3:26	54	29/3/2017 4:31	54	30/3/2017 5:36	56	31/3/2017 6:41	61	1/4/2017 7:46	59	3/4/2017 0:51	56		
28/3/2017 3:31	54	29/3/2017 4:36	55	30/3/2017 5:41	57	31/3/2017 6:46	61	1/4/2017 7:51	59	3/4/2017 0:56	55		
28/3/2017 3:36	54	29/3/2017 4:41	55	30/3/2017 5:46	57	31/3/2017 6:51	61	1/4/2017 7:56	60	3/4/2017 1:01	57		
28/3/2017 3:41	54	29/3/2017 4:46	54	30/3/2017 5:51	58	31/3/2017 6:56	61	2/4/2017 0:01	59	3/4/2017 1:06	56		
28/3/2017 3:46	55	29/3/2017 4:51	55	30/3/2017 5:56	56	31/3/2017 7:01	54	2/4/2017 0:06	59				

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
3/4/2017 4:16	54	4/4/2017 5:21	56	5/4/2017 6:26	55	6/4/2017 23:31	59	8/4/2017 0:36	59	9/4/2017 1:41	57
3/4/2017 4:21	55	4/4/2017 5:26	55	5/4/2017 6:31	60	6/4/2017 23:36	59	8/4/2017 0:41	58	9/4/2017 1:46	57
3/4/2017 4:26	56	4/4/2017 5:31	56	5/4/2017 6:36	45	6/4/2017 23:41	59	8/4/2017 0:46	58	9/4/2017 1:51	57
3/4/2017 4:31	55	4/4/2017 5:36	56	5/4/2017 6:41	61	6/4/2017 23:46	59	8/4/2017 0:51	58	9/4/2017 1:56	57
3/4/2017 4:36	54	4/4/2017 5:41	55	5/4/2017 6:46	60	6/4/2017 23:51	59	8/4/2017 0:56	58	9/4/2017 2:01	57
3/4/2017 4:41	55	4/4/2017 5:46	56	5/4/2017 6:51	59	6/4/2017 23:56	59	8/4/2017 1:01	58	9/4/2017 2:06	56
3/4/2017 4:46	54	4/4/2017 5:51	57	5/4/2017 6:56	59	7/4/2017 0:01	59	8/4/2017 1:06	58	9/4/2017 2:11	56
3/4/2017 4:51	55	4/4/2017 5:56	57	5/4/2017 23:01	58	7/4/2017 0:06	59	8/4/2017 1:11	58	9/4/2017 2:16	57
3/4/2017 4:56	54	4/4/2017 6:01	58	5/4/2017 23:06	59	7/4/2017 0:11	59	8/4/2017 1:16	57	9/4/2017 2:21	56
3/4/2017 5:01	55	4/4/2017 6:06	58	5/4/2017 23:11	58	7/4/2017 0:16	59	8/4/2017 1:21	58	9/4/2017 2:26	56
3/4/2017 5:06	55	4/4/2017 6:11	58	5/4/2017 23:16	58	7/4/2017 0:21	58	8/4/2017 1:26	57	9/4/2017 2:31	57
3/4/2017 5:11	54	4/4/2017 6:16	58	5/4/2017 23:21	58	7/4/2017 0:26	59	8/4/2017 1:31	57	9/4/2017 2:36	56
3/4/2017 5:16	55	4/4/2017 6:21	58	5/4/2017 23:26	59	7/4/2017 0:31	59	8/4/2017 1:36	58	9/4/2017 2:41	56
3/4/2017 5:21	56	4/4/2017 6:26	59	5/4/2017 23:31	59	7/4/2017 0:36	58	8/4/2017 1:41	57	9/4/2017 2:46	55
3/4/2017 5:26	56	4/4/2017 6:31	60	5/4/2017 23:36	58	7/4/2017 0:41	59	8/4/2017 1:46	57	9/4/2017 2:51	56
3/4/2017 5:31	56	4/4/2017 6:36	58	5/4/2017 23:41	58	7/4/2017 0:46	59	8/4/2017 1:51	57	9/4/2017 2:56	55
3/4/2017 5:36	56	4/4/2017 6:41	60	5/4/2017 23:46	58	7/4/2017 0:51	58	8/4/2017 1:56	57	9/4/2017 3:01	55
3/4/2017 5:41	57	4/4/2017 6:46	59	5/4/2017 23:51	57	7/4/2017 0:56	58	8/4/2017 2:01	56	9/4/2017 3:06	55
3/4/2017 5:46	57	4/4/2017 6:51	59	5/4/2017 23:56	58	7/4/2017 1:01	59	8/4/2017 2:06	56	9/4/2017 3:11	55
3/4/2017 5:51	57	4/4/2017 6:56	58	6/4/2017 0:01	58	7/4/2017 1:06	57	8/4/2017 2:11	56	9/4/2017 3:16	55
3/4/2017 5:56	58	4/4/2017 23:01	58	6/4/2017 0:06	59	7/4/2017 1:11	58	8/4/2017 2:16	56	9/4/2017 3:21	56
3/4/2017 6:01	57	4/4/2017 23:06	58	6/4/2017 0:11	58	7/4/2017 1:16	58	8/4/2017 2:21	58	9/4/2017 3:26	56
3/4/2017 6:06	59	4/4/2017 23:11	59	6/4/2017 0:16	59	7/4/2017 1:21	59	8/4/2017 2:26	56	9/4/2017 3:31	56
3/4/2017 6:11	59	4/4/2017 23:16	58	6/4/2017 0:21	58	7/4/2017 1:26	58	8/4/2017 2:31	58	9/4/2017 3:36	58
3/4/2017 6:16	59	4/4/2017 23:21	57	6/4/2017 0:26	60	7/4/2017 1:31	57	8/4/2017 2:36	56	9/4/2017 3:41	55
3/4/2017 6:21	59	4/4/2017 23:26	58	6/4/2017 0:31	58	7/4/2017 1:36	58	8/4/2017 2:41	56	9/4/2017 3:46	55
3/4/2017 6:26	60	4/4/2017 23:31	58	6/4/2017 0:36	58	7/4/2017 1:41	58	8/4/2017 2:46	56	9/4/2017 3:51	56
3/4/2017 6:31	61	4/4/2017 23:36	58	6/4/2017 0:41	57	7/4/2017 1:46	57	8/4/2017 2:51	56	9/4/2017 3:56	56
3/4/2017 6:36	43	4/4/2017 23:41	57	6/4/2017 0:46	57	7/4/2017 1:51	58	8/4/2017 2:56	56	9/4/2017 4:01	55
3/4/2017 6:41	61	4/4/2017 23:46	60	6/4/2017 0:51	56	7/4/2017 1:56	57	8/4/2017 3:01	55	9/4/2017 4:06	55
3/4/2017 6:46	61	4/4/2017 23:51	57	6/4/2017 0:56	56	7/4/2017 2:01	57	8/4/2017 3:06	57	9/4/2017 4:11	55
3/4/2017 6:51	61	4/4/2017 23:56	57	6/4/2017 1:01	56	7/4/2017 2:06	58	8/4/2017 3:11	56	9/4/2017 4:16	56
3/4/2017 6:56	54	5/4/2017 0:01	58	6/4/2017 1:06	57	7/4/2017 2:11	57	8/4/2017 3:16	56	9/4/2017 4:21	56
3/4/2017 23:01	59	5/4/2017 0:06	57	6/4/2017 1:11	57	7/4/2017 2:16	58	8/4/2017 3:21	56	9/4/2017 4:26	56
3/4/2017 23:06	59	5/4/2017 0:11	57	6/4/2017 1:16	56	7/4/2017 2:21	58	8/4/2017 3:26	55	9/4/2017 4:31	56
3/4/2017 23:11	59	5/4/2017 0:16	57	6/4/2017 1:21	56	7/4/2017 2:26	57	8/4/2017 3:31	56	9/4/2017 4:36	55
3/4/2017 23:16	59	5/4/2017 0:21	57	6/4/2017 1:26	56	7/4/2017 2:31	58	8/4/2017 3:36	55	9/4/2017 4:41	55
3/4/2017 23:21	59	5/4/2017 0:26	57	6/4/2017 1:31	55	7/4/2017 2:36	57	8/4/2017 3:41	56	9/4/2017 4:46	55
3/4/2017 23:26	58	5/4/2017 0:31	57	6/4/2017 1:36	56	7/4/2017 2:41	57	8/4/2017 3:46	56	9/4/2017 4:51	55
3/4/2017 23:31	59	5/4/2017 0:36	56	6/4/2017 1:41	60	7/4/2017 2:46	57	8/4/2017 3:51	56	9/4/2017 4:56	54
3/4/2017 23:36	58	5/4/2017 0:41	55	6/4/2017 1:46	55	7/4/2017 2:51	58	8/4/2017 3:56	56	9/4/2017 5:01	55
3/4/2017 23:41	59	5/4/2017 0:46	57	6/4/2017 1:51	56	7/4/2017 2:56	57	8/4/2017 4:01	55	9/4/2017 5:06	54
3/4/2017 23:46	58	5/4/2017 0:51	55	6/4/2017 1:56	55	7/4/2017 3:01	58	8/4/2017 4:06	55	9/4/2017 5:11	55
3/4/2017 23:51	59	5/4/2017 0:56	57	6/4/2017 2:01	56	7/4/2017 3:06	58	8/4/2017 4:11	55	9/4/2017 5:16	55
3/4/2017 23:56	58	5/4/2017 1:01	55	6/4/2017 2:06	55	7/4/2017 3:11	57	8/4/2017 4:16	56	9/4/2017 5:21	56
4/4/2017 0:01	58	5/4/2017 1:06	57	6/4/2017 2:11	55	7/4/2017 3:16	58	8/4/2017 4:21	55	9/4/2017 5:26	56
4/4/2017 0:06	58	5/4/2017 1:11	56	6/4/2017 2:16	54	7/4/2017 3:21	57	8/4/2017 4:26	57	9/4/2017 5:31	56
4/4/2017 0:11	58	5/4/2017 1:16	57	6/4/2017 2:21	55	7/4/2017 3:26	57	8/4/2017 4:31	56	9/4/2017 5:36	57
4/4/2017 0:16	59	5/4/2017 1:21	55	6/4/2017 2:26	55	7/4/2017 3:31	56	8/4/2017 4:36	56	9/4/2017 5:41	57
4/4/2017 0:21	59	5/4/2017 1:26	58	6/4/2017 2:31	55	7/4/2017 3:36	56	8/4/2017 4:41	55	9/4/2017 5:46	56
4/4/2017 0:26	58	5/4/2017 1:31	55	6/4/2017 2:36	54	7/4/2017 3:41	56	8/4/2017 4:46	55	9/4/2017 5:51	57
4/4/2017 0:31	58	5/4/2017 1:36	56	6/4/2017 2:41	54	7/4/2017 3:46	57	8/4/2017 4:51	56	9/4/2017 5:56	57
4/4/2017 0:36	58	5/4/2017 1:41	54	6/4/2017 2:46	55	7/4/2017 3:51	57	8/4/2017 4:56	56	9/4/2017 6:01	57
4/4/2017 0:41	58	5/4/2017 1:46	55	6/4/2017 2:51	56	7/4/2017 3:56	58	8/4/2017 5:01	56	9/4/2017 6:06	57
4/4/2017 0:46	59	5/4/2017 1:51	54	6/4/2017 2:56	55	7/4/2017 4:01	58	8/4/2017 5:06	56	9/4/2017 6:11	57
4/4/2017 0:51	57	5/4/2017 1:56	55	6/4/2017 3:01	53	7/4/2017 4:06	57	8/4/2017 5:11	55	9/4/2017 6:16	58
4/4/2017 0:56	57	5/4/2017 2:01	56	6/4/2017 3:06	54	7/4/2017 4:11	57	8/4/2017 5:16	55	9/4/2017 6:21	58
4/4/2017 1:01	59	5/4/2017 2:06	53	6/4/2017 3:11	54	7/4/2017 4:16	57	8/4/2017 5:21	56	9/4/2017 6:26	59
4/4/2017 1:06	57	5/4/2017 2:11	56	6/4/2017 3:16	53	7/4/2017 4:21	57	8/4/2017 5:26	56	9/4/2017 6:31	58
4/4/2017 1:11	57	5/4/2017 2:16	55	6/4/2017 3:21	55	7/4/2017 4:26	58	8/4/2017 5:31	55	9/4/2017 6:36	59
4/4/2017 1:16	57	5/4/2017 2:21	54	6/4/2017 3:26	53	7/4/2017 4:31	57	8/4/2017 5:36	56	9/4/2017 6:41	59
4/4/2017 1:21	57	5/4/2017 2:26	54	6/4/2017 3:31	55	7/4/2017 4:36	56	8/4/2017 5:41	57	9/4/2017 6:46	59
4/4/2017 1:26	57	5/4/2017 2:31	57	6/4/2017 3:36	54	7/4/2017 4:41	57	8/4/2017 5:46	57	9/4/2017 6:51	60
4/4/2017 1:31	57	5/4/2017 2:36	54	6/4/2017 3:41	54	7/4/2017 4:46	57	8/4/2017 5:51	57	9/4/2017 6:56	54
4/4/2017 1:36	58	5/4/2017 2:41	55	6/4/2017 3:46	54	7/4/2017 4:51	58	8/4/2017 5:56	57	9/4/2017 23:01	59
4/4/2017 1:41	56	5/4/2017 2:46	54	6/4/2017 3:51	54	7/4/2017 4:56	57	8/4/2017 6:01	57	9/4/2017 23:06	58
4/4/2017 1:46	57	5/4/2017 2:51	55	6/4/2017 3:56	54	7/4/2017 5:01	57	8/4/2017 6:06	58	9/4/2017 23:11	58
4/4/2017 1:51	57	5/4/2017 2:56	53	6/4/2017 4:01	54	7/4/2017 5:06	57	8/4/2017 6:11	57	9/4/2017 23:16	58
4/4/2017 1:56	56	5/4/2017 3:01	55	6/4/2017 4:06	53	7/4/2017 5:11	58	8/4/2017 6:16	59	9/4/2017 23:21	59
4/4/2017 2:01	56	5/4/2017 3:06	57	6/4/2017 4:11	54	7/4/2017 5:16	58	8/4/2017 6:21	59	9/4/2017 23:26	58
4/4/2017 2:06	57	5/4/2017 3:11	53	6/4/2017 4:16	53	7/4/2017 5:21	58	8/4/2017 6:26	59	9/4/2017 23:31	58
4/4/2017 2:11	56	5/4/2017 3:16	54	6/4/2017 4:21	54	7/4/2017 5:26	58	8/4/2017 6:31	60	9/4/2017 23:36	58
4/4/2017 2:16	57	5/4/2017 3:21	57	6/4/2017 4:26	54	7/4/2017 5:31	58	8/4/2017 6:36	59	9/4/2017 23:41	58
4/4/2017 2:21	56	5/4/2017 3:26	54	6/4/2017 4:31	54	7/4/2017 5:36	58	8/4/2017 6:41	60	9/4/2017 23:46	58
4/4/2017 2:26	57	5/4/2017 3:31	54	6/4/2017 4:36	54	7/4/2017 5:41	58	8/4/2017 6:46	50	9/4/2017 23:51	58
4/4/2017 2:31	56	5/4/2017 3:36	53	6/4/2017 4:41	55	7/4/2017 5:46	59	8/4/2017 6:51	60	9/4/2017 23:56	58
4/4/2017 2:36	56	5/4/2017 3:41	54	6/4/2017 4:46	54	7/4/2017 5:51	58	8/4/2017 6:56	61	10/4/2017 0:01	57
4/4/2017 2:41	56	5/4/2017 3:46	54	6/4/2017 4:51	54	7/4/2017 5:56	59	8/4/2017 23:01	59	10/4/2017 0:06	57
4/4/2017 2:46	56	5/4/2017 3:51	54	6/4/2017 4:56	54						

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)											
10/4/2017 2:46	55	11/4/2017 3:51	55	12/4/2017 4:56	55	13/4/2017 6:01	59	14/4/2017 23:06	58	16/4/2017 0:11	57		
10/4/2017 2:51	53	11/4/2017 3:56	56	12/4/2017 5:01	55	13/4/2017 6:06	60	14/4/2017 23:11	59	16/4/2017 0:16	56		
10/4/2017 2:56	55	11/4/2017 4:01	54	12/4/2017 5:06	55	13/4/2017 6:11	60	14/4/2017 23:16	59	16/4/2017 0:21	56		
10/4/2017 3:01	53	11/4/2017 4:06	56	12/4/2017 5:11	55	13/4/2017 6:16	61	14/4/2017 23:21	59	16/4/2017 0:26	56		
10/4/2017 3:06	54	11/4/2017 4:11	54	12/4/2017 5:16	55	13/4/2017 6:21	60	14/4/2017 23:26	58	16/4/2017 0:31	56		
10/4/2017 3:11	54	11/4/2017 4:16	54	12/4/2017 5:21	56	13/4/2017 6:26	60	14/4/2017 23:31	60	16/4/2017 0:36	56		
10/4/2017 3:16	53	11/4/2017 4:21	55	12/4/2017 5:26	56	13/4/2017 6:31	45	14/4/2017 23:36	57	16/4/2017 0:41	56		
10/4/2017 3:21	54	11/4/2017 4:26	56	12/4/2017 5:31	57	13/4/2017 6:36	45	14/4/2017 23:41	58	16/4/2017 0:46	56		
10/4/2017 3:26	53	11/4/2017 4:31	55	12/4/2017 5:36	56	13/4/2017 6:41	55	14/4/2017 23:46	58	16/4/2017 0:51	56		
10/4/2017 3:31	56	11/4/2017 4:36	55	12/4/2017 5:41	57	13/4/2017 6:46	55	14/4/2017 23:51	57	16/4/2017 0:56	55		
10/4/2017 3:36	55	11/4/2017 4:41	54	12/4/2017 5:46	56	13/4/2017 6:51	55	14/4/2017 23:56	58	16/4/2017 1:01	56		
10/4/2017 3:41	56	11/4/2017 4:46	54	12/4/2017 5:51	57	13/4/2017 6:56	55	15/4/2017 0:01	58	16/4/2017 1:06	56		
10/4/2017 3:46	54	11/4/2017 4:51	55	12/4/2017 5:56	56	13/4/2017 23:01	61	15/4/2017 0:06	57	16/4/2017 1:11	58		
10/4/2017 3:51	54	11/4/2017 4:56	55	12/4/2017 6:01	57	13/4/2017 23:06	59	15/4/2017 0:11	57	16/4/2017 1:16	56		
10/4/2017 3:56	55	11/4/2017 5:01	55	12/4/2017 6:06	58	13/4/2017 23:11	59	15/4/2017 0:16	56	16/4/2017 1:21	56		
10/4/2017 4:01	54	11/4/2017 5:06	55	12/4/2017 6:11	59	13/4/2017 23:16	59	15/4/2017 0:21	57	16/4/2017 1:26	56		
10/4/2017 4:06	55	11/4/2017 5:11	56	12/4/2017 6:16	59	13/4/2017 23:21	59	15/4/2017 0:26	56	16/4/2017 1:31	56		
10/4/2017 4:11	54	11/4/2017 5:16	56	12/4/2017 6:21	59	13/4/2017 23:26	59	15/4/2017 0:31	57	16/4/2017 1:36	56		
10/4/2017 4:16	54	11/4/2017 5:21	56	12/4/2017 6:26	59	13/4/2017 23:31	59	15/4/2017 0:36	56	16/4/2017 1:41	56		
10/4/2017 4:21	54	11/4/2017 5:26	56	12/4/2017 6:31	60	13/4/2017 23:36	59	15/4/2017 0:41	57	16/4/2017 1:46	55		
10/4/2017 4:26	56	11/4/2017 5:31	57	12/4/2017 6:36	59	13/4/2017 23:41	60	15/4/2017 0:46	57	16/4/2017 1:51	56		
10/4/2017 4:31	54	11/4/2017 5:36	57	12/4/2017 6:41	60	13/4/2017 23:46	59	15/4/2017 0:51	56	16/4/2017 1:56	55		
10/4/2017 4:36	54	11/4/2017 5:41	57	12/4/2017 6:46	61	13/4/2017 23:51	59	15/4/2017 0:56	56	16/4/2017 2:01	54		
10/4/2017 4:41	55	11/4/2017 5:46	57	12/4/2017 6:51	59	13/4/2017 23:56	59	15/4/2017 1:01	56	16/4/2017 2:06	58		
10/4/2017 4:46	54	11/4/2017 5:51	57	12/4/2017 6:56	54	14/4/2017 0:01	57	15/4/2017 1:06	57	16/4/2017 2:11	55		
10/4/2017 4:51	55	11/4/2017 5:56	57	12/4/2017 23:01	60	14/4/2017 0:06	57	15/4/2017 1:11	59	16/4/2017 2:16	56		
10/4/2017 4:56	55	11/4/2017 6:01	57	12/4/2017 23:06	60	14/4/2017 0:11	57	15/4/2017 1:16	57	16/4/2017 2:21	56		
10/4/2017 5:01	55	11/4/2017 6:06	58	12/4/2017 23:11	54	14/4/2017 0:16	57	15/4/2017 1:21	58	16/4/2017 2:26	57		
10/4/2017 5:06	55	11/4/2017 6:11	58	12/4/2017 23:16	60	14/4/2017 0:21	57	15/4/2017 1:26	56	16/4/2017 2:31	55		
10/4/2017 5:11	55	11/4/2017 6:16	59	12/4/2017 23:21	60	14/4/2017 0:26	57	15/4/2017 1:31	56	16/4/2017 2:36	56		
10/4/2017 5:16	55	11/4/2017 6:21	59	12/4/2017 23:26	60	14/4/2017 0:31	57	15/4/2017 1:36	56	16/4/2017 2:41	56		
10/4/2017 5:21	56	11/4/2017 6:26	60	12/4/2017 23:31	60	14/4/2017 0:36	57	15/4/2017 1:41	55	16/4/2017 2:46	56		
10/4/2017 5:26	56	11/4/2017 6:31	59	12/4/2017 23:36	60	14/4/2017 0:41	57	15/4/2017 1:46	56	16/4/2017 2:51	56		
10/4/2017 5:31	57	11/4/2017 6:36	60	12/4/2017 23:41	60	14/4/2017 0:46	57	15/4/2017 1:51	56	16/4/2017 2:56	56		
10/4/2017 5:36	56	11/4/2017 6:41	60	12/4/2017 23:46	60	14/4/2017 0:51	57	15/4/2017 1:56	56	16/4/2017 3:01	55		
10/4/2017 5:41	57	11/4/2017 6:46	61	12/4/2017 23:51	60	14/4/2017 0:56	57	15/4/2017 2:01	56	16/4/2017 3:06	55		
10/4/2017 5:46	56	11/4/2017 6:51	60	12/4/2017 23:56	60	14/4/2017 1:01	57	15/4/2017 2:06	56	16/4/2017 3:11	54		
10/4/2017 5:51	58	11/4/2017 6:56	60	13/4/2017 0:01	60	14/4/2017 1:06	57	15/4/2017 2:11	55	16/4/2017 3:16	55		
10/4/2017 5:56	57	11/4/2017 23:01	60	13/4/2017 0:06	59	14/4/2017 1:11	57	15/4/2017 2:16	56	16/4/2017 3:21	55		
10/4/2017 6:01	57	11/4/2017 23:06	59	13/4/2017 0:11	60	14/4/2017 1:16	56	15/4/2017 2:21	56	16/4/2017 3:26	54		
10/4/2017 6:06	58	11/4/2017 23:11	60	13/4/2017 0:16	59	14/4/2017 1:21	56	15/4/2017 2:26	56	16/4/2017 3:31	57		
10/4/2017 6:11	59	11/4/2017 23:16	60	13/4/2017 0:21	60	14/4/2017 1:26	58	15/4/2017 2:31	56	16/4/2017 3:36	55		
10/4/2017 6:16	58	11/4/2017 23:21	59	13/4/2017 0:26	59	14/4/2017 1:31	57	15/4/2017 2:36	57	16/4/2017 3:41	54		
10/4/2017 6:21	59	11/4/2017 23:26	59	13/4/2017 0:31	60	14/4/2017 1:36	56	15/4/2017 2:41	55	16/4/2017 3:46	55		
10/4/2017 6:26	59	11/4/2017 23:31	59	13/4/2017 0:36	59	14/4/2017 1:41	57	15/4/2017 2:46	55	16/4/2017 3:51	55		
10/4/2017 6:31	60	11/4/2017 23:36	59	13/4/2017 0:41	60	14/4/2017 1:46	57	15/4/2017 2:51	55	16/4/2017 3:56	55		
10/4/2017 6:36	60	11/4/2017 23:41	59	13/4/2017 0:46	52	14/4/2017 1:51	57	15/4/2017 2:56	56	16/4/2017 4:01	55		
10/4/2017 6:41	60	11/4/2017 23:46	59	13/4/2017 0:51	60	14/4/2017 1:56	57	15/4/2017 3:01	56	16/4/2017 4:06	54		
10/4/2017 6:46	60	11/4/2017 23:51	58	13/4/2017 0:56	59	14/4/2017 2:01	57	15/4/2017 3:06	55	16/4/2017 4:11	55		
10/4/2017 6:51	47	11/4/2017 23:56	57	13/4/2017 1:01	59	14/4/2017 2:06	57	15/4/2017 3:11	55	16/4/2017 4:16	54		
10/4/2017 6:56	61	12/4/2017 0:01	58	13/4/2017 1:06	59	14/4/2017 2:11	57	15/4/2017 3:16	56	16/4/2017 4:21	56		
10/4/2017 23:01	59	12/4/2017 0:06	57	13/4/2017 1:11	59	14/4/2017 2:16	56	15/4/2017 3:21	56	16/4/2017 4:26	56		
10/4/2017 23:06	59	12/4/2017 0:11	57	13/4/2017 1:16	59	14/4/2017 2:21	56	15/4/2017 3:26	57	16/4/2017 4:31	55		
10/4/2017 23:11	59	12/4/2017 0:16	57	13/4/2017 1:21	59	14/4/2017 2:26	56	15/4/2017 3:31	56	16/4/2017 4:36	54		
10/4/2017 23:16	60	12/4/2017 0:21	57	13/4/2017 1:26	59	14/4/2017 2:31	55	15/4/2017 3:36	56	16/4/2017 4:41	55		
10/4/2017 23:21	58	12/4/2017 0:26	57	13/4/2017 1:31	59	14/4/2017 2:36	57	15/4/2017 3:41	57	16/4/2017 4:46	55		
10/4/2017 23:26	58	12/4/2017 0:31	57	13/4/2017 1:36	59	14/4/2017 2:41	56	15/4/2017 3:46	59	16/4/2017 4:51	56		
10/4/2017 23:31	58	12/4/2017 0:36	57	13/4/2017 1:41	59	14/4/2017 2:46	56	15/4/2017 3:51	58	16/4/2017 4:56	55		
10/4/2017 23:36	59	12/4/2017 0:41	56	13/4/2017 1:46	59	14/4/2017 2:51	56	15/4/2017 3:56	55	16/4/2017 5:01	56		
10/4/2017 23:41	59	12/4/2017 0:46	57	13/4/2017 1:51	59	14/4/2017 2:56	57	15/4/2017 4:01	55	16/4/2017 5:06	56		
10/4/2017 23:46	58	12/4/2017 0:51	57	13/4/2017 1:56	59	14/4/2017 3:01	56	15/4/2017 4:06	55	16/4/2017 5:11	56		
10/4/2017 23:51	58	12/4/2017 0:56	57	13/4/2017 2:01	59	14/4/2017 3:06	56	15/4/2017 4:11	56	16/4/2017 5:16	55		
10/4/2017 23:56	58	12/4/2017 1:01	57	13/4/2017 2:06	59	14/4/2017 3:11	56	15/4/2017 4:16	55	16/4/2017 5:21	56		
11/4/2017 0:01	58	12/4/2017 1:06	57	13/4/2017 2:11	59	14/4/2017 3:16	56	15/4/2017 4:21	56	16/4/2017 5:26	56		
11/4/2017 0:06	57	12/4/2017 1:11	57	13/4/2017 2:16	59	14/4/2017 3:21	56	15/4/2017 4:26	57	16/4/2017 5:31	55		
11/4/2017 0:11	58	12/4/2017 1:16	56	13/4/2017 2:21	58	14/4/2017 3:26	56	15/4/2017 4:31	57	16/4/2017 5:36	55		
11/4/2017 0:16	58	12/4/2017 1:21	56	13/4/2017 2:26	58	14/4/2017 3:31	56	15/4/2017 4:36	55	16/4/2017 5:41	56		
11/4/2017 0:21	57	12/4/2017 1:26	56	13/4/2017 2:31	57	14/4/2017 3:36	56	15/4/2017 4:41	55	16/4/2017 5:46	57		
11/4/2017 0:26	57	12/4/2017 1:31	56	13/4/2017 2:36	57	14/4/2017 3:41	56	15/4/2017 4:46	56	16/4/2017 5:51	56		
11/4/2017 0:31	58	12/4/2017 1:36	57	13/4/2017 2:41	58	14/4/2017 3:46	57	15/4/2017 4:51	57	16/4/2017 5:56	58		
11/4/2017 0:36	58	12/4/2017 1:41	56	13/4/2017 2:46	57	14/4/2017 3:51	56	15/4/2017 4:56	55	16/4/2017 6:01	57		
11/4/2017 0:41	57	12/4/2017 1:46	55	13/4/2017 2:51	58	14/4/2017 3:56	57	15/4/2017 5:01</					

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)											
17/4/2017 1:16	56	18/4/2017 2:21	55	19/4/2017 3:26	58	20/4/2017 4:31	55	21/4/2017 5:36	58	22/4/2017 6:41	60		
17/4/2017 1:21	57	18/4/2017 2:26	55	19/4/2017 3:31	58	20/4/2017 4:36	55	21/4/2017 5:41	58	22/4/2017 6:46	59		
17/4/2017 1:26	56	18/4/2017 2:31	54	19/4/2017 3:36	59	20/4/2017 4:41	56	21/4/2017 5:46	59	22/4/2017 6:51	60		
17/4/2017 1:31	55	18/4/2017 2:36	56	19/4/2017 3:41	58	20/4/2017 4:46	56	21/4/2017 5:51	59	22/4/2017 6:56	60		
17/4/2017 1:36	55	18/4/2017 2:41	55	19/4/2017 3:46	58	20/4/2017 4:51	56	21/4/2017 5:56	58	22/4/2017 7:01	59		
17/4/2017 1:41	57	18/4/2017 2:46	54	19/4/2017 3:51	58	20/4/2017 4:56	55	21/4/2017 6:01	58	22/4/2017 7:06	59		
17/4/2017 1:46	55	18/4/2017 2:51	55	19/4/2017 3:56	58	20/4/2017 5:01	55	21/4/2017 6:06	51	22/4/2017 7:11	59		
17/4/2017 1:51	54	18/4/2017 2:56	54	19/4/2017 4:01	58	20/4/2017 5:06	56	21/4/2017 6:11	60	22/4/2017 7:16	59		
17/4/2017 1:56	55	18/4/2017 3:01	54	19/4/2017 4:06	58	20/4/2017 5:11	56	21/4/2017 6:16	48	22/4/2017 7:21	59		
17/4/2017 2:01	55	18/4/2017 3:06	53	19/4/2017 4:11	58	20/4/2017 5:16	55	21/4/2017 6:21	60	22/4/2017 7:26	59		
17/4/2017 2:06	55	18/4/2017 3:11	54	19/4/2017 4:16	58	20/4/2017 5:21	56	21/4/2017 6:26	39	22/4/2017 7:31	59		
17/4/2017 2:11	55	18/4/2017 3:16	54	19/4/2017 4:21	57	20/4/2017 5:26	57	21/4/2017 6:31	51	22/4/2017 7:36	59		
17/4/2017 2:16	55	18/4/2017 3:21	53	19/4/2017 4:26	58	20/4/2017 5:31	57	21/4/2017 6:36	61	22/4/2017 7:41	59		
17/4/2017 2:21	55	18/4/2017 3:26	54	19/4/2017 4:31	58	20/4/2017 5:36	57	21/4/2017 6:41	60	22/4/2017 7:46	58		
17/4/2017 2:26	56	18/4/2017 3:31	54	19/4/2017 4:36	57	20/4/2017 5:41	57	21/4/2017 6:46	56	22/4/2017 7:51	59		
17/4/2017 2:31	56	18/4/2017 3:36	54	19/4/2017 4:41	57	20/4/2017 5:46	57	21/4/2017 6:51	51	22/4/2017 7:56	59		
17/4/2017 2:36	55	18/4/2017 3:41	54	19/4/2017 4:46	57	20/4/2017 5:51	59	21/4/2017 6:56	47	23/4/2017 0:01	59		
17/4/2017 2:41	55	18/4/2017 3:46	55	19/4/2017 4:51	58	20/4/2017 5:56	58	21/4/2017 7:01	60	23/4/2017 0:06	60		
17/4/2017 2:46	54	18/4/2017 3:51	53	19/4/2017 4:56	58	20/4/2017 6:01	58	21/4/2017 7:06	59	23/4/2017 0:11	58		
17/4/2017 2:51	54	18/4/2017 3:56	54	19/4/2017 5:01	58	20/4/2017 6:06	59	21/4/2017 7:11	59	23/4/2017 0:16	59		
17/4/2017 2:56	55	18/4/2017 4:01	53	19/4/2017 5:06	58	20/4/2017 6:11	60	21/4/2017 7:16	60	23/4/2017 0:21	59		
17/4/2017 3:01	55	18/4/2017 4:06	54	19/4/2017 5:11	58	20/4/2017 6:16	59	21/4/2017 7:21	59	23/4/2017 0:26	58		
17/4/2017 3:06	55	18/4/2017 4:11	55	19/4/2017 5:16	58	20/4/2017 6:21	60	21/4/2017 7:26	59	23/4/2017 0:31	58		
17/4/2017 3:11	54	18/4/2017 4:16	54	19/4/2017 5:21	58	20/4/2017 6:26	60	21/4/2017 7:31	59	23/4/2017 0:36	59		
17/4/2017 3:16	55	18/4/2017 4:21	54	19/4/2017 5:26	58	20/4/2017 6:31	60	21/4/2017 7:36	60	23/4/2017 0:41	59		
17/4/2017 3:21	55	18/4/2017 4:26	55	19/4/2017 5:31	59	20/4/2017 6:36	42	21/4/2017 7:41	59	23/4/2017 0:46	58		
17/4/2017 3:26	55	18/4/2017 4:31	55	19/4/2017 5:36	59	20/4/2017 6:41	56	21/4/2017 7:46	59	23/4/2017 0:51	58		
17/4/2017 3:31	55	18/4/2017 4:36	54	19/4/2017 5:41	60	20/4/2017 6:46	42	21/4/2017 7:51	58	23/4/2017 0:56	58		
17/4/2017 3:36	54	18/4/2017 4:41	55	19/4/2017 5:46	59	20/4/2017 6:51	49	21/4/2017 7:56	58	23/4/2017 1:01	58		
17/4/2017 3:41	54	18/4/2017 4:46	55	19/4/2017 5:51	60	20/4/2017 6:56	60	22/4/2017 0:01	58	23/4/2017 1:06	57		
17/4/2017 3:46	55	18/4/2017 4:51	56	19/4/2017 5:56	61	20/4/2017 7:01	61	22/4/2017 0:06	59	23/4/2017 1:11	57		
17/4/2017 3:51	55	18/4/2017 4:56	56	19/4/2017 6:01	60	20/4/2017 7:06	51	22/4/2017 0:11	59	23/4/2017 1:16	58		
17/4/2017 3:56	54	18/4/2017 5:01	54	19/4/2017 6:06	60	20/4/2017 7:11	47	22/4/2017 0:16	58	23/4/2017 1:21	58		
17/4/2017 4:01	54	18/4/2017 5:06	56	19/4/2017 6:11	60	20/4/2017 7:16	60	22/4/2017 0:21	58	23/4/2017 1:26	57		
17/4/2017 4:06	55	18/4/2017 5:11	55	19/4/2017 6:16	60	20/4/2017 7:21	59	22/4/2017 0:26	58	23/4/2017 1:31	59		
17/4/2017 4:11	53	18/4/2017 5:16	55	19/4/2017 6:21	53	20/4/2017 7:26	59	22/4/2017 0:31	59	23/4/2017 1:36	57		
17/4/2017 4:16	55	18/4/2017 5:21	55	19/4/2017 6:26	45	20/4/2017 7:31	59	22/4/2017 0:36	58	23/4/2017 1:41	58		
17/4/2017 4:21	54	18/4/2017 5:26	55	19/4/2017 6:31	52	20/4/2017 7:36	58	22/4/2017 0:41	58	23/4/2017 1:46	57		
17/4/2017 4:26	57	18/4/2017 5:31	57	19/4/2017 6:36	52	20/4/2017 7:41	59	22/4/2017 0:46	58	23/4/2017 1:51	57		
17/4/2017 4:31	55	18/4/2017 5:36	57	19/4/2017 6:41	57	20/4/2017 7:46	59	22/4/2017 0:51	58	23/4/2017 1:56	57		
17/4/2017 4:36	55	18/4/2017 5:41	56	19/4/2017 6:46	55	20/4/2017 7:51	60	22/4/2017 0:56	58	23/4/2017 2:01	56		
17/4/2017 4:41	55	18/4/2017 5:46	58	19/4/2017 6:51	54	20/4/2017 7:56	60	22/4/2017 1:01	58	23/4/2017 2:06	57		
17/4/2017 4:46	54	18/4/2017 5:51	58	19/4/2017 6:56	55	21/4/2017 0:01	58	22/4/2017 1:06	58	23/4/2017 2:11	57		
17/4/2017 4:51	55	18/4/2017 5:56	58	19/4/2017 7:01	59	21/4/2017 0:06	59	22/4/2017 1:11	57	23/4/2017 2:16	57		
17/4/2017 4:56	55	18/4/2017 6:01	58	19/4/2017 7:06	58	21/4/2017 0:11	59	22/4/2017 1:16	58	23/4/2017 2:21	57		
17/4/2017 5:01	55	18/4/2017 6:06	59	19/4/2017 7:11	59	21/4/2017 0:16	58	22/4/2017 1:21	57	23/4/2017 2:26	56		
17/4/2017 5:06	55	18/4/2017 6:11	59	19/4/2017 7:16	59	21/4/2017 0:21	58	22/4/2017 1:26	58	23/4/2017 2:31	56		
17/4/2017 5:11	56	18/4/2017 6:16	60	19/4/2017 7:21	58	21/4/2017 0:26	59	22/4/2017 1:31	57	23/4/2017 2:36	56		
17/4/2017 5:16	55	18/4/2017 6:21	59	19/4/2017 7:26	58	21/4/2017 0:31	59	22/4/2017 1:36	58	23/4/2017 2:41	57		
17/4/2017 5:21	56	18/4/2017 6:26	60	19/4/2017 7:31	58	21/4/2017 0:36	59	22/4/2017 1:41	57	23/4/2017 2:46	57		
17/4/2017 5:26	56	18/4/2017 6:31	61	19/4/2017 7:36	58	21/4/2017 0:41	57	22/4/2017 1:46	58	23/4/2017 2:51	57		
17/4/2017 5:31	56	18/4/2017 6:36	60	19/4/2017 7:41	58	21/4/2017 0:46	56	22/4/2017 1:51	57	23/4/2017 2:56	57		
17/4/2017 5:36	57	18/4/2017 6:41	47	19/4/2017 7:46	58	21/4/2017 0:51	57	22/4/2017 1:56	58	23/4/2017 3:01	56		
17/4/2017 5:41	57	18/4/2017 6:46	55	19/4/2017 7:51	58	21/4/2017 0:56	57	22/4/2017 2:01	57	23/4/2017 3:06	56		
17/4/2017 5:46	57	18/4/2017 6:51	61	19/4/2017 7:56	58	21/4/2017 1:01	56	22/4/2017 2:06	58	23/4/2017 3:11	55		
17/4/2017 5:51	58	18/4/2017 6:56	43	20/4/2017 0:01	59	21/4/2017 1:06	57	22/4/2017 2:11	56	23/4/2017 3:16	56		
17/4/2017 5:56	57	18/4/2017 7:01	61	20/4/2017 0:06	58	21/4/2017 1:11	58	22/4/2017 2:16	57	23/4/2017 3:21	56		
17/4/2017 6:01	57	18/4/2017 7:06	60	20/4/2017 0:11	58	21/4/2017 1:16	58	22/4/2017 2:21	58	23/4/2017 3:26	56		
17/4/2017 6:06	59	18/4/2017 7:11	60	20/4/2017 0:16	57	21/4/2017 1:21	56	22/4/2017 2:26	58	23/4/2017 3:31	55		
17/4/2017 6:11	57	18/4/2017 7:16	60	20/4/2017 0:21	56	21/4/2017 1:26	57	22/4/2017 2:31	57	23/4/2017 3:36	57		
17/4/2017 6:16	58	18/4/2017 7:21	60	20/4/2017 0:26	57	21/4/2017 1:31	57	22/4/2017 2:36	56	23/4/2017 3:41	55		
17/4/2017 6:21	58	18/4/2017 7:26	60	20/4/2017 0:31	57	21/4/2017 1:36	57	22/4/2017 2:41	58	23/4/2017 3:46	56		
17/4/2017 6:26	60	18/4/2017 7:31	60	20/4/2017 0:36	58	21/4/2017 1:41	56	22/4/2017 2:46	57	23/4/2017 3:51	56		
17/4/2017 6:31	60	18/4/2017 7:36	60	20/4/2017 0:41	57	21/4/2017 1:46	56	22/4/2017 2:51	56	23/4/2017 3:56	65		
17/4/2017 6:36	60	18/4/2017 7:41	60	20/4/2017 0:46	57	21/4/2017 1:51	57	22/4/2017 2:56	56	23/4/2017 4:01	56		
17/4/2017 6:41	60	18/4/2017 7:46	60	20/4/2017 0:51	56	21/4/2017 1:56	57	22/4/2017 3:01	56	23/4/2017 4:06	56		
17/4/2017 6:46	58	18/4/2017 7:51	60	20/4/2017 0:56	57	21/4/2017 2:01	57	22/4/2017 3:06	57	23/4/2017 4:11	56		
17/4/2017 6:51	59	18/4/2017 7:56	59	20/4/2017 1:01	56	21/4/2017 2:06	56	22/4/2017 3:11	56	23/4/2017 4:16	55		
17/4/2017 6:56	58	19/4/2017 0:01	60	20/4/2017 1:06	57	21/4/2017 2:11	57	22/4/2017 3:16	56	23/4/2017 4:21	55		
17/4/2017 7:01	58	19/4/2017 0:06	60	20/4/2017 1:11	56	21/4/2017 2:16	57	22/4/2017 3:21	56	23/4/2017 4:26	56		
17/4/2017 7:06	58	19/4/2017 0:11	59	20/4/2017 1:16	55	21/4/2017 2:21	56	22/4/2017 3:26	57	23/4/2017 4:31	57		
17/4/2017 7:11	59	19/4/2017 0:16	59	20/4/2017 1:21	56	21/4/2017 2:26	55	22/4/2017 3:31	56	23/4/2017 4:36	56		
17/4/2017													

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)	
23/4/2017 23:46	57	25/4/2017 0:51	59
23/4/2017 23:51	58	25/4/2017 0:56	59
23/4/2017 23:56	58	25/4/2017 1:01	58
24/4/2017 0:01	56	25/4/2017 1:06	59
24/4/2017 0:06	57	25/4/2017 1:11	58
24/4/2017 0:11	58	25/4/2017 1:16	59
24/4/2017 0:16	57	25/4/2017 1:21	59
24/4/2017 0:21	57	25/4/2017 1:26	59
24/4/2017 0:26	58	25/4/2017 1:31	58
24/4/2017 0:31	57	25/4/2017 1:36	58
24/4/2017 0:36	56	25/4/2017 1:41	59
24/4/2017 0:41	55	25/4/2017 1:46	58
24/4/2017 0:46	57	25/4/2017 1:51	58
24/4/2017 0:51	57	25/4/2017 1:56	58
24/4/2017 0:56	56	25/4/2017 2:01	58
24/4/2017 1:01	56	25/4/2017 2:06	58
24/4/2017 1:06	56	25/4/2017 2:11	58
24/4/2017 1:11	57	25/4/2017 2:16	58
24/4/2017 1:16	56	25/4/2017 2:21	58
24/4/2017 1:21	56	25/4/2017 2:26	58
24/4/2017 1:26	55	25/4/2017 2:31	58
24/4/2017 1:31	56	25/4/2017 2:36	58
24/4/2017 1:36	55	25/4/2017 2:41	58
24/4/2017 1:41	54	25/4/2017 2:46	58
24/4/2017 1:46	54	25/4/2017 2:51	58
24/4/2017 1:51	55	25/4/2017 2:56	58
24/4/2017 1:56	55	25/4/2017 3:01	58
24/4/2017 2:01	56	25/4/2017 3:06	57
24/4/2017 2:06	55	25/4/2017 3:11	58
24/4/2017 2:11	54	25/4/2017 3:16	57
24/4/2017 2:16	54	25/4/2017 3:21	58
24/4/2017 2:21	54	25/4/2017 3:26	58
24/4/2017 2:26	54	25/4/2017 3:31	58
24/4/2017 2:31	54	25/4/2017 3:36	59
24/4/2017 2:36	54	25/4/2017 3:41	58
24/4/2017 2:41	54	25/4/2017 3:46	58
24/4/2017 2:46	53	25/4/2017 3:51	58
24/4/2017 2:51	54	25/4/2017 3:56	58
24/4/2017 2:56	54	25/4/2017 4:01	58
24/4/2017 3:01	55	25/4/2017 4:06	59
24/4/2017 3:06	53	25/4/2017 4:11	58
24/4/2017 3:11	55	25/4/2017 4:16	58
24/4/2017 3:16	55	25/4/2017 4:21	59
24/4/2017 3:21	53	25/4/2017 4:26	58
24/4/2017 3:26	55	25/4/2017 4:31	58
24/4/2017 3:31	54	25/4/2017 4:36	59
24/4/2017 3:36	54	25/4/2017 4:41	58
24/4/2017 3:41	53	25/4/2017 4:46	58
24/4/2017 3:46	54	25/4/2017 4:51	58
24/4/2017 3:51	54	25/4/2017 4:56	59
24/4/2017 3:56	55	25/4/2017 5:01	58
24/4/2017 4:01	54	25/4/2017 5:06	58
24/4/2017 4:06	54	25/4/2017 5:11	59
24/4/2017 4:11	54	25/4/2017 5:16	59
24/4/2017 4:16	55	25/4/2017 5:21	59
24/4/2017 4:21	56	25/4/2017 5:26	59
24/4/2017 4:26	55	25/4/2017 5:31	59
24/4/2017 4:31	53	25/4/2017 5:36	59
24/4/2017 4:36	54	25/4/2017 5:41	60
24/4/2017 4:41	54	25/4/2017 5:46	60
24/4/2017 4:46	54	25/4/2017 5:51	58
24/4/2017 4:51	57	25/4/2017 5:56	60
24/4/2017 4:56	55	25/4/2017 6:01	60
24/4/2017 5:01	54	25/4/2017 6:06	43
24/4/2017 5:06	56	25/4/2017 6:11	60
24/4/2017 5:11	55	25/4/2017 6:16	47
24/4/2017 5:16	55	25/4/2017 6:21	50
24/4/2017 5:21	56	25/4/2017 6:26	53
24/4/2017 5:26	56	25/4/2017 6:31	44
24/4/2017 5:31	56	25/4/2017 6:36	53
24/4/2017 5:36	57	25/4/2017 6:41	54
24/4/2017 5:41	58	25/4/2017 6:46	54
24/4/2017 5:46	59	25/4/2017 6:51	52
24/4/2017 5:51	59	25/4/2017 6:56	61
24/4/2017 5:56	57	25/4/2017 23:01	59
24/4/2017 6:01	58	25/4/2017 23:06	60
24/4/2017 6:06	59	25/4/2017 23:11	59
24/4/2017 6:11	59	25/4/2017 23:16	59
24/4/2017 6:16	60	25/4/2017 23:21	59
24/4/2017 6:21	59	25/4/2017 23:26	59
24/4/2017 6:26	60	25/4/2017 23:31	58
24/4/2017 6:31	60	25/4/2017 23:36	58
24/4/2017 6:36	39	25/4/2017 23:41	58
24/4/2017 6:41	61	25/4/2017 23:46	58
24/4/2017 6:46	53	25/4/2017 23:51	58
24/4/2017 6:51	48	25/4/2017 23:56	58
24/4/2017 6:56	60	26/4/2017 0:01	58
24/4/2017 23:01	44	26/4/2017 0:06	57
24/4/2017 23:06	60	26/4/2017 0:11	58
24/4/2017 23:11	60	26/4/2017 0:16	58
24/4/2017 23:16	60	26/4/2017 0:21	58
24/4/2017 23:21	60	26/4/2017 0:26	58
24/4/2017 23:26	60	26/4/2017 0:31	57
24/4/2017 23:31	60	26/4/2017 0:36	57
24/4/2017 23:36	60	26/4/2017 0:41	57
24/4/2017 23:41	60	26/4/2017 0:46	57
24/4/2017 23:46	59	26/4/2017 0:51	56
24/4/2017 23:51	38	26/4/2017 0:56	57
24/4/2017 23:56	60	26/4/2017 1:01	57
25/4/2017 0:01	59	26/4/2017 1:06	57
25/4/2017 0:06	60	26/4/2017 1:11	57
25/4/2017 0:11	59	26/4/2017 1:16	56
25/4/2017 0:16	59	26/4/2017 1:21	57
25/4/2017 0:21	59	26/4/2017 1:26	56
25/4/2017 0:26	60	26/4/2017 1:31	56
25/4/2017 0:31	59	26/4/2017 1:36	55
25/4/2017 0:36	59	26/4/2017 1:41	57
25/4/2017 0:41	59	26/4/2017 1:46	57
25/4/2017 0:46	58	26/4/2017 1:51	56

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
Normal Day 07:00-19:00		4/5/2017 13:01 67	67	10/5/2017 7:31 65	65	15/5/2017 14:01 67	67	20/5/2017 8:31 68	68	25/5/2017 15:01 67	67
27/4/2017 7:01	64	4/5/2017 13:31 67	67	10/5/2017 8:01 65	65	15/5/2017 14:31 67	67	20/5/2017 9:01 69	69	25/5/2017 15:31 68	68
27/4/2017 7:31	66	4/5/2017 14:01 68	68	10/5/2017 8:31 66	66	15/5/2017 15:01 68	68	20/5/2017 9:31 67	67	25/5/2017 16:01 66	66
27/4/2017 8:01	65	4/5/2017 14:31 67	67	10/5/2017 9:01 67	67	15/5/2017 15:31 67	67	20/5/2017 10:01 67	67	25/5/2017 16:31 66	66
27/4/2017 8:31	65	4/5/2017 15:01 66	66	10/5/2017 9:31 67	67	15/5/2017 16:01 66	66	20/5/2017 10:31 69	69	25/5/2017 17:01 66	66
27/4/2017 9:01	66	4/5/2017 15:31 66	66	10/5/2017 10:01 66	66	15/5/2017 16:31 67	67	20/5/2017 11:01 71	71	25/5/2017 17:31 66	66
27/4/2017 9:31	66	4/5/2017 16:01 67	67	10/5/2017 10:31 67	67	15/5/2017 17:01 67	67	20/5/2017 11:31 68	68	25/5/2017 18:01 66	66
27/4/2017 10:01	67	4/5/2017 16:31 67	67	10/5/2017 11:01 66	66	15/5/2017 17:31 67	67	20/5/2017 12:01 66	66	25/5/2017 18:31 66	66
27/4/2017 10:31	66	4/5/2017 17:01 66	66	10/5/2017 11:31 66	66	15/5/2017 18:01 67	67	20/5/2017 12:31 66	66	26/5/2017 7:01 64	64
27/4/2017 11:01	66	4/5/2017 17:31 67	67	10/5/2017 12:01 66	66	15/5/2017 18:31 66	66	20/5/2017 13:01 68	68	26/5/2017 7:31 64	64
27/4/2017 11:31	66	4/5/2017 18:01 67	67	10/5/2017 12:31 66	66	16/5/2017 7:01 65	65	20/5/2017 13:31 70	70	26/5/2017 8:01 65	65
27/4/2017 12:01	67	4/5/2017 18:31 67	67	10/5/2017 13:01 66	66	16/5/2017 7:31 66	66	20/5/2017 14:01 70	70	26/5/2017 8:31 65	65
27/4/2017 12:31	66	5/5/2017 7:01 64	64	10/5/2017 13:31 66	66	16/5/2017 8:01 67	67	20/5/2017 14:31 70	70	26/5/2017 9:01 66	66
27/4/2017 13:01	67	5/5/2017 7:31 65	65	10/5/2017 14:01 66	66	16/5/2017 8:31 66	66	20/5/2017 15:01 70	70	26/5/2017 9:31 66	66
27/4/2017 13:31	67	5/5/2017 8:01 66	66	10/5/2017 14:31 66	66	16/5/2017 9:01 65	65	20/5/2017 15:31 69	69	26/5/2017 10:01 66	66
27/4/2017 14:01	68	5/5/2017 8:31 66	66	10/5/2017 15:01 66	66	16/5/2017 9:31 66	66	20/5/2017 16:01 69	69	26/5/2017 10:31 67	67
27/4/2017 14:31	67	5/5/2017 9:01 66	66	10/5/2017 15:31 66	66	16/5/2017 10:01 67	67	20/5/2017 16:31 67	67	26/5/2017 11:01 67	67
27/4/2017 15:01	66	5/5/2017 9:31 66	66	10/5/2017 16:01 66	66	16/5/2017 10:31 68	68	20/5/2017 17:01 67	67	26/5/2017 11:31 66	66
27/4/2017 15:31	67	5/5/2017 10:01 66	66	10/5/2017 16:31 66	66	16/5/2017 11:01 67	67	20/5/2017 17:31 65	65	26/5/2017 12:01 66	66
27/4/2017 16:01	67	5/5/2017 10:31 67	67	10/5/2017 17:01 66	66	16/5/2017 11:31 66	66	20/5/2017 18:01 65	65	26/5/2017 12:31 66	66
27/4/2017 16:31	67	5/5/2017 11:01 66	66	10/5/2017 17:31 65	65	16/5/2017 12:01 66	66	20/5/2017 18:31 65	65	26/5/2017 13:01 66	66
27/4/2017 17:01	67	5/5/2017 11:31 66	66	10/5/2017 18:01 66	66	16/5/2017 12:31 67	67	22/5/2017 7:01 64	64	26/5/2017 13:31 67	67
27/4/2017 17:31	66	5/5/2017 12:01 66	66	10/5/2017 18:31 66	66	16/5/2017 13:01 67	67	22/5/2017 7:31 66	66	26/5/2017 14:01 67	67
27/4/2017 18:01	66	5/5/2017 12:31 66	66	11/5/2017 7:01 64	64	16/5/2017 13:31 67	67	22/5/2017 8:01 67	67	26/5/2017 14:31 67	67
27/4/2017 18:31	66	5/5/2017 13:01 66	66	11/5/2017 7:31 65	65	16/5/2017 14:01 67	67	22/5/2017 8:31 67	67	26/5/2017 15:01 67	67
28/4/2017 7:01	64	5/5/2017 13:31 67	67	11/5/2017 8:01 66	66	16/5/2017 14:31 67	67	22/5/2017 9:01 67	67	26/5/2017 15:31 67	67
28/4/2017 7:31	66	5/5/2017 14:01 66	66	11/5/2017 8:31 65	65	16/5/2017 15:01 66	66	22/5/2017 9:31 68	68	26/5/2017 16:01 67	67
28/4/2017 8:01	66	5/5/2017 14:31 66	66	11/5/2017 9:01 65	65	16/5/2017 15:31 67	67	22/5/2017 10:01 67	67	26/5/2017 16:31 67	67
28/4/2017 8:31	66	5/5/2017 15:01 66	66	11/5/2017 9:31 66	66	16/5/2017 16:01 67	67	22/5/2017 10:31 69	69	26/5/2017 17:01 67	67
28/4/2017 9:01	66	5/5/2017 15:31 66	66	11/5/2017 10:01 67	67	16/5/2017 16:31 67	67	22/5/2017 11:01 69	69	26/5/2017 17:31 66	66
28/4/2017 9:31	66	5/5/2017 16:01 66	66	11/5/2017 10:31 67	67	16/5/2017 17:01 67	67	22/5/2017 11:31 67	67	26/5/2017 18:01 66	66
28/4/2017 10:01	66	5/5/2017 16:31 66	66	11/5/2017 11:01 67	67	16/5/2017 17:31 67	67	22/5/2017 12:01 66	66	26/5/2017 18:31 66	66
28/4/2017 10:31	67	5/5/2017 17:01 66	66	11/5/2017 11:31 66	66	16/5/2017 18:01 67	67	22/5/2017 12:31 67	67		
28/4/2017 11:01	66	5/5/2017 17:31 66	66	11/5/2017 12:01 66	66	16/5/2017 18:31 66	66	22/5/2017 13:01 67	67	Normal Day 19:00-23:00	
28/4/2017 11:31	66	5/5/2017 18:01 66	66	11/5/2017 12:31 65	65	17/5/2017 7:01 64	64	22/5/2017 13:31 68	68	Sunday & Holiday	
28/4/2017 12:01	66	5/5/2017 18:31 65	65	11/5/2017 13:01 66	66	17/5/2017 7:31 65	65	22/5/2017 14:01 68	68	07:00-23:00	
28/4/2017 12:31	66	6/5/2017 7:01 63	63	11/5/2017 13:31 66	66	17/5/2017 8:01 66	66	22/5/2017 14:31 68	68		
28/4/2017 13:01	66	6/5/2017 7:31 65	65	11/5/2017 14:01 66	66	17/5/2017 8:31 65	65	22/5/2017 15:01 67	67	27/4/2017 19:01	65
28/4/2017 13:31	67	6/5/2017 8:01 66	66	11/5/2017 14:31 66	66	17/5/2017 9:01 66	66	22/5/2017 15:31 67	67	27/4/2017 19:06	65
28/4/2017 14:01	67	6/5/2017 8:31 66	66	11/5/2017 15:01 66	66	17/5/2017 9:31 65	65	22/5/2017 16:01 67	67	27/4/2017 19:11	66
28/4/2017 14:31	67	6/5/2017 9:01 66	66	11/5/2017 15:31 65	65	17/5/2017 10:01 65	65	22/5/2017 16:31 67	67	27/4/2017 19:16	65
28/4/2017 15:01	67	6/5/2017 9:31 67	67	11/5/2017 16:01 66	66	17/5/2017 10:31 66	66	22/5/2017 17:01 67	67	27/4/2017 19:21	65
28/4/2017 15:31	67	6/5/2017 10:01 67	67	11/5/2017 16:31 66	66	17/5/2017 11:01 66	66	22/5/2017 17:31 67	67	27/4/2017 19:26	65
28/4/2017 16:01	67	6/5/2017 10:31 66	66	11/5/2017 17:01 65	65	17/5/2017 11:31 67	67	22/5/2017 18:01 67	67	27/4/2017 19:31	64
28/4/2017 16:31	67	6/5/2017 11:01 66	66	11/5/2017 17:31 66	66	17/5/2017 12:01 66	66	22/5/2017 18:31 66	66	27/4/2017 19:36	64
28/4/2017 17:01	66	6/5/2017 11:31 66	66	11/5/2017 18:01 66	66	17/5/2017 12:31 66	66	23/5/2017 7:01 65	65	27/4/2017 19:41	63
28/4/2017 17:31	66	6/5/2017 12:01 65	65	11/5/2017 18:31 64	64	17/5/2017 13:01 66	66	23/5/2017 7:31 66	66	27/4/2017 19:46	63
28/4/2017 18:01	66	6/5/2017 12:31 65	65	12/5/2017 7:01 64	64	17/5/2017 13:31 66	66	23/5/2017 8:01 66	66	27/4/2017 19:51	64
28/4/2017 18:31	66	6/5/2017 13:01 66	66	12/5/2017 7:31 65	65	17/5/2017 14:01 66	66	23/5/2017 8:31 65	65	27/4/2017 19:56	63
29/4/2017 7:01	63	6/5/2017 13:31 65	65	12/5/2017 8:01 66	66	17/5/2017 14:31 65	65	23/5/2017 9:01 66	66	27/4/2017 20:01	63
29/4/2017 7:31	65	6/5/2017 14:01 65	65	12/5/2017 8:31 65	65	17/5/2017 15:01 66	66	23/5/2017 9:31 67	67	27/4/2017 20:06	64
29/4/2017 8:01	67	6/5/2017 14:31 65	65	12/5/2017 9:01 65	65	17/5/2017 15:31 66	66	23/5/2017 10:01 67	67	27/4/2017 20:11	64
29/4/2017 8:31	67	6/5/2017 15:01 65	65	12/5/2017 9:31 66	66	17/5/2017 16:01 66	66	23/5/2017 10:31 66	66	27/4/2017 20:16	65
29/4/2017 9:01	66	6/5/2017 15:31 66	66	12/5/2017 10:01 66	66	17/5/2017 16:31 67	67	23/5/2017 11:01 66	66	27/4/2017 20:21	64
29/4/2017 9:31	67	6/5/2017 16:01 65	65	12/5/2017 10:31 66	66	17/5/2017 17:01 66	66	23/5/2017 11:31 64	64	27/4/2017 20:26	64
29/4/2017 10:01	67	6/5/2017 16:31 65	65	12/5/2017 11:01 66	66	17/5/2017 17:31 66	66	23/5/2017 12:01 65	65	27/4/2017 20:31	64
29/4/2017 10:31	67	6/5/2017 17:01 65	65	12/5/2017 11:31 66	66	17/5/2017 18:01 66	66	23/5/2017 12:31 65	65	27/4/2017 20:36	64
29/4/2017 11:01	66	6/5/2017 17:31 65	65	12/5/2017 12:01 66	66	17/5/2017 18:31 66	66	23/5/2017 13:01 68	68	27/4/2017 20:41	64
29/4/2017 11:31	66	6/5/2017 18:01 65	65	12/5/2017 12:31 65	65	18/5/2017 7:01 63	63	23/5/2017 13:31 68	68	27/4/2017 20:46	64
29/4/2017 12:01	66	6/5/2017 18:31 65	65	12/5/2017 13:01 66	66	18/5/2017 7:31 65	65	23/5/2017 14:01 69	69	27/4/2017 20:51	64
29/4/2017 12:31	65	8/5/2017 7:01 64	64	12/5/2017 13:31 66	66	18/5/2017 8:01 66	66	23/5/2017 14:31 67	67	27/4/2017 20:56	64
29/4/2017 13:01	65	8/5/2017 7:31 65	65	12/5/2017 14:01 66	66	18/5/2017 8:31 65	65	23/5/2017 15:01 67	67	27/4/2017 21:01	64
29/4/2017 13:31	66	8/5/2017 8:01 66	66	12/5/2017 14:31 66	66	18/5/2017 9:01 65	65	23/5/2017 15:31 66	66	27/4/2017 21:06	64
29/4/2017 14:01	66	8/5/2017 8:31 66	66	12/5/2017 15:01 66	66	18/5/2017 9:31 67	67	23/5/2017 16:01 68	68	27/4/2017 21:11	64
29/4/2017 14:31	65	8/5/2017 9:01 66	66	12/5/2017 15:31 66	66	18/5/2017 10:01 67	67	23/5/2017 16:31 67	67	27/4/2017 21:16	63
29/4/2017 15:01	66	8/5/2017 9:31 67	67	12/5/2017 16:01 66	66	18/5/2017 10:31 67	67	23/5/2017 17:01 67	67	27/4/2017 21:21	65
29/4/2017 15:31	65	8/5/2017 10:01 66	66	12/5/2017 16:31 66	66	18/5/2017 11:01 67	67	23/5/2017 17:31 66	66	27/4/2017 21:26	64
29/4/2017 16:01	66	8/5/2017 10:31 67	67	12/5/2017 17:01 66	66	18/5/2017 11:31 66	66	23/5/2017 18:01 66	66	27/4/2017 21:31	64
29/4/2017 16:31	67	8/5/2017 11:01 67	67	12/5/2017 17:31 66	66	18/5/2017 12:01 66	66	23/5/2017 18:31 67	67	27/4/2017 21:36	63
29/4/2017 17:01	67	8/5/2017 11:31 66	66	12/5/2017 18:01 66	66	18/5/2017 12:31 66	66	24/5/2017 7:01 70	70	27/4/2017 21:41	64
29/4/2017 17:31											

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
28/4/2017 21:01	64	30/4/2017 10:06	64	30/4/2017 19:11	64	1/5/2017 12:16	62	1/5/2017 21:21	62	3/5/2017 10:26	65
28/4/2017 21:06	64	30/4/2017 10:11	66	30/4/2017 19:16	63	1/5/2017 12:21	63	1/5/2017 21:26	62	3/5/2017 10:31	65
28/4/2017 21:11	63	30/4/2017 10:16	64	30/4/2017 19:21	64	1/5/2017 12:26	63	1/5/2017 21:31	63	3/5/2017 10:36	64
28/4/2017 21:16	64	30/4/2017 10:21	63	30/4/2017 19:26	64	1/5/2017 12:31	63	1/5/2017 21:36	63	3/5/2017 10:41	64
28/4/2017 21:21	64	30/4/2017 10:26	64	30/4/2017 19:31	63	1/5/2017 12:36	63	1/5/2017 21:41	62	3/5/2017 10:46	64
28/4/2017 21:26	64	30/4/2017 10:31	63	30/4/2017 19:36	63	1/5/2017 12:41	63	1/5/2017 21:46	62	3/5/2017 10:51	63
28/4/2017 21:31	64	30/4/2017 10:36	64	30/4/2017 19:41	64	1/5/2017 12:46	64	1/5/2017 21:51	63	3/5/2017 10:56	63
28/4/2017 21:36	63	30/4/2017 10:41	63	30/4/2017 19:46	63	1/5/2017 12:51	63	1/5/2017 21:56	62	3/5/2017 11:01	63
28/4/2017 21:41	64	30/4/2017 10:46	63	30/4/2017 19:51	64	1/5/2017 12:56	63	1/5/2017 22:01	63	3/5/2017 11:06	63
28/4/2017 21:46	63	30/4/2017 10:51	63	30/4/2017 19:56	63	1/5/2017 13:01	64	1/5/2017 22:06	62	3/5/2017 11:11	63
28/4/2017 21:51	66	30/4/2017 10:56	64	30/4/2017 20:01	63	1/5/2017 13:06	64	1/5/2017 22:11	62	3/5/2017 11:16	63
28/4/2017 21:56	63	30/4/2017 11:01	63	30/4/2017 20:06	63	1/5/2017 13:11	63	1/5/2017 22:16	63	3/5/2017 11:21	63
28/4/2017 22:01	63	30/4/2017 11:06	63	30/4/2017 20:11	63	1/5/2017 13:16	63	1/5/2017 22:21	62	3/5/2017 11:26	63
28/4/2017 22:06	64	30/4/2017 11:11	63	30/4/2017 20:16	63	1/5/2017 13:21	63	1/5/2017 22:26	62	3/5/2017 11:31	63
28/4/2017 22:11	64	30/4/2017 11:16	63	30/4/2017 20:21	63	1/5/2017 13:26	63	1/5/2017 22:31	62	3/5/2017 11:36	62
28/4/2017 22:16	64	30/4/2017 11:21	63	30/4/2017 20:26	63	1/5/2017 13:31	63	1/5/2017 22:36	62	3/5/2017 11:41	65
28/4/2017 22:21	63	30/4/2017 11:26	63	30/4/2017 20:31	62	1/5/2017 13:36	66	1/5/2017 22:41	62	3/5/2017 11:46	63
28/4/2017 22:26	64	30/4/2017 11:31	63	30/4/2017 20:36	63	1/5/2017 13:41	63	1/5/2017 22:46	62	3/5/2017 11:51	63
28/4/2017 22:31	64	30/4/2017 11:36	63	30/4/2017 20:41	63	1/5/2017 13:46	63	1/5/2017 22:51	62	3/5/2017 11:56	64
28/4/2017 22:36	65	30/4/2017 11:41	64	30/4/2017 20:46	62	1/5/2017 13:51	63	1/5/2017 22:56	63	3/5/2017 12:01	64
28/4/2017 22:41	65	30/4/2017 11:46	63	30/4/2017 20:51	63	1/5/2017 13:56	63	2/5/2017 19:01	65	3/5/2017 12:06	62
28/4/2017 22:46	63	30/4/2017 11:51	63	30/4/2017 20:56	64	1/5/2017 14:01	63	2/5/2017 19:06	66	3/5/2017 12:11	63
28/4/2017 22:51	64	30/4/2017 11:56	62	30/4/2017 21:01	65	1/5/2017 14:06	63	2/5/2017 19:11	66	3/5/2017 12:16	63
28/4/2017 22:56	63	30/4/2017 12:01	63	30/4/2017 21:06	63	1/5/2017 14:11	63	2/5/2017 19:16	66	3/5/2017 12:21	62
29/4/2017 19:01	64	30/4/2017 12:06	63	30/4/2017 21:11	63	1/5/2017 14:16	64	2/5/2017 19:21	66	3/5/2017 12:26	63
29/4/2017 19:06	64	30/4/2017 12:11	64	30/4/2017 21:16	62	1/5/2017 14:21	63	2/5/2017 19:26	65	3/5/2017 12:31	63
29/4/2017 19:11	64	30/4/2017 12:16	64	30/4/2017 21:21	63	1/5/2017 14:26	63	2/5/2017 19:31	65	3/5/2017 12:36	63
29/4/2017 19:16	64	30/4/2017 12:21	64	30/4/2017 21:26	62	1/5/2017 14:31	65	2/5/2017 19:36	65	3/5/2017 12:41	63
29/4/2017 19:21	64	30/4/2017 12:26	63	30/4/2017 21:31	63	1/5/2017 14:36	63	2/5/2017 19:41	63	3/5/2017 12:46	64
29/4/2017 19:26	64	30/4/2017 12:31	64	30/4/2017 21:36	63	1/5/2017 14:41	63	2/5/2017 19:46	63	3/5/2017 12:51	64
29/4/2017 19:31	65	30/4/2017 12:36	65	30/4/2017 21:41	63	1/5/2017 14:46	63	2/5/2017 19:51	64	3/5/2017 12:56	64
29/4/2017 19:36	64	30/4/2017 12:41	65	30/4/2017 21:46	63	1/5/2017 14:51	63	2/5/2017 19:56	63	3/5/2017 13:01	64
29/4/2017 19:41	64	30/4/2017 12:46	65	30/4/2017 21:51	64	1/5/2017 14:56	63	2/5/2017 20:01	65	3/5/2017 13:06	64
29/4/2017 19:46	62	30/4/2017 12:51	65	30/4/2017 21:56	62	1/5/2017 15:01	64	2/5/2017 20:06	63	3/5/2017 13:11	63
29/4/2017 19:51	63	30/4/2017 12:56	66	30/4/2017 22:01	63	1/5/2017 15:06	64	2/5/2017 20:11	63	3/5/2017 13:16	63
29/4/2017 19:56	67	30/4/2017 13:01	65	30/4/2017 22:06	63	1/5/2017 15:11	64	2/5/2017 20:16	64	3/5/2017 13:21	64
29/4/2017 20:01	63	30/4/2017 13:06	64	30/4/2017 22:11	63	1/5/2017 15:16	64	2/5/2017 20:21	63	3/5/2017 13:26	64
29/4/2017 20:06	63	30/4/2017 13:11	63	30/4/2017 22:16	63	1/5/2017 15:21	64	2/5/2017 20:26	63	3/5/2017 13:31	64
29/4/2017 20:11	65	30/4/2017 13:16	62	30/4/2017 22:21	64	1/5/2017 15:26	63	2/5/2017 20:31	63	3/5/2017 13:36	64
29/4/2017 20:16	63	30/4/2017 13:21	63	30/4/2017 22:26	63	1/5/2017 15:31	66	2/5/2017 20:36	63	3/5/2017 13:41	64
29/4/2017 20:21	63	30/4/2017 13:26	63	30/4/2017 22:31	62	1/5/2017 15:36	64	2/5/2017 20:41	64	3/5/2017 13:46	64
29/4/2017 20:26	63	30/4/2017 13:31	63	30/4/2017 22:36	63	1/5/2017 15:41	63	2/5/2017 20:46	63	3/5/2017 13:51	64
29/4/2017 20:31	64	30/4/2017 13:36	63	30/4/2017 22:41	63	1/5/2017 15:46	64	2/5/2017 20:51	64	3/5/2017 13:56	64
29/4/2017 20:36	64	30/4/2017 13:41	64	30/4/2017 22:46	62	1/5/2017 15:51	63	2/5/2017 20:56	63	3/5/2017 14:01	63
29/4/2017 20:41	63	30/4/2017 13:46	64	30/4/2017 22:51	62	1/5/2017 15:56	64	2/5/2017 21:01	63	3/5/2017 14:06	66
29/4/2017 20:46	62	30/4/2017 13:51	63	30/4/2017 22:56	63	1/5/2017 16:01	63	2/5/2017 21:06	63	3/5/2017 14:11	64
29/4/2017 20:51	63	30/4/2017 13:56	64	1/5/2017 7:01	61	1/5/2017 16:06	64	2/5/2017 21:11	63	3/5/2017 14:16	64
29/4/2017 20:56	63	30/4/2017 14:01	64	1/5/2017 7:06	61	1/5/2017 16:11	64	2/5/2017 21:16	63	3/5/2017 14:21	64
29/4/2017 21:01	63	30/4/2017 14:06	64	1/5/2017 7:11	62	1/5/2017 16:16	64	2/5/2017 21:21	62	3/5/2017 14:26	64
29/4/2017 21:06	64	30/4/2017 14:11	64	1/5/2017 7:16	62	1/5/2017 16:21	64	2/5/2017 21:26	64	3/5/2017 14:31	64
29/4/2017 21:11	63	30/4/2017 14:16	64	1/5/2017 7:21	62	1/5/2017 16:26	63	2/5/2017 21:31	63	3/5/2017 14:36	63
29/4/2017 21:16	64	30/4/2017 14:21	63	1/5/2017 7:26	61	1/5/2017 16:31	69	2/5/2017 21:36	62	3/5/2017 14:41	64
29/4/2017 21:21	63	30/4/2017 14:26	63	1/5/2017 7:31	61	1/5/2017 16:36	63	2/5/2017 21:41	62	3/5/2017 14:46	64
29/4/2017 21:26	63	30/4/2017 14:31	64	1/5/2017 7:36	62	1/5/2017 16:41	63	2/5/2017 21:46	63	3/5/2017 14:51	64
29/4/2017 21:31	64	30/4/2017 14:36	64	1/5/2017 7:41	62	1/5/2017 16:46	63	2/5/2017 21:51	64	3/5/2017 14:56	64
29/4/2017 21:36	63	30/4/2017 14:41	64	1/5/2017 7:46	63	1/5/2017 16:51	64	2/5/2017 21:56	63	3/5/2017 15:01	64
29/4/2017 21:41	63	30/4/2017 14:46	64	1/5/2017 7:51	62	1/5/2017 16:56	63	2/5/2017 22:01	62	3/5/2017 15:06	64
29/4/2017 21:46	63	30/4/2017 14:51	64	1/5/2017 7:56	61	1/5/2017 17:01	64	2/5/2017 22:06	63	3/5/2017 15:11	64
29/4/2017 21:51	64	30/4/2017 14:56	64	1/5/2017 8:01	64	1/5/2017 17:06	63	2/5/2017 22:11	64	3/5/2017 15:16	63
29/4/2017 21:56	64	30/4/2017 15:01	64	1/5/2017 8:06	61	1/5/2017 17:11	63	2/5/2017 22:16	63	3/5/2017 15:21	64
29/4/2017 22:01	63	30/4/2017 15:06	63	1/5/2017 8:11	62	1/5/2017 17:16	63	2/5/2017 22:21	63	3/5/2017 15:26	64
29/4/2017 22:06	63	30/4/2017 15:11	64	1/5/2017 8:16	63	1/5/2017 17:21	64	2/5/2017 22:26	64	3/5/2017 15:31	65
29/4/2017 22:11	63	30/4/2017 15:16	64	1/5/2017 8:21	63	1/5/2017 17:26	64	2/5/2017 22:31	65	3/5/2017 15:36	63
29/4/2017 22:16	63	30/4/2017 15:21	64	1/5/2017 8:26	63	1/5/2017 17:31	63	2/5/2017 22:36	63	3/5/2017 15:41	64
29/4/2017 22:21	63	30/4/2017 15:26	65	1/5/2017 8:31	63	1/5/2017 17:36	63	2/5/2017 22:41	62	3/5/2017 15:46	64
29/4/2017 22:26	63	30/4/2017 15:31	64	1/5/2017 8:36	64	1/5/2017 17:41	63	2/5/2017 22:46	63	3/5/2017 15:51	64
29/4/2017 22:31	63	30/4/2017 15:36	65	1/5/2017 8:41	64	1/5/2017 17:46	64	2/5/2017 22:51	63	3/5/2017 15:56	64
29/4/2017 22:36	64	30/4/2017 15:41	65	1/5/2017 8:46	63	1/5/2017 17:51	63	2/5/2017 22:56	63	3/5/2017 16:01	64
29/4/2017 22:41	64	30/4/2017 15:46	64	1/5/2017 8:51	63	1/5/2017 17:56	63	3/5/2017 7:01	61	3/5/2017 16:06	63
29/4/2017 22:46	63	30/4/2017 15:51	65	1/5/2017 8:56	63	1/5/2017 18:01	65	3/5/2017 7:06	68	3/5/2017 16:11	64
29/4/2017 22:51	63	30/4/2017 15:56	65	1/5/2017 9:01	63	1/5/2017 18:06	63	3/5/2017 7:11	61	3/5/2017 16:16	64
29/4/2017 22:56	63	30/4/2017 16:01	65	1/5/2017 9:06	64	1/5/2017 18:11	63	3/5/2017 7:16	62	3/5/2017 16:21	64
30/4/2017 7:01	61	30/4/2017 16:06	65	1/5/2017 9:11	64	1/5/2017 18:16	64	3/5/2017 7:21	62	3/5/2017 16:26	63
30/4/2017 7:06	62	30/4/2017 16:11	66	1/5/2017 9:16	64	1/5/2017 18:21	67	3/5/2017 7:26	62	3/5/2017 16:31	63
30/4/2017 7:11	63	30/4/2017 16:16	67	1/5/2017 9:21	63	1/5/2017 18:26	63	3/5/2017 7:31	61	3/5/2017 16:36	

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
3/5/2017 19:31	63	5/5/2017 20:36	63	7/5/2017 9:41	63	7/5/2017 18:46	64	9/5/2017 19:51	64	11/5/2017 20:56	63
3/5/2017 19:36	63	5/5/2017 20:41	64	7/5/2017 9:46	63	7/5/2017 18:51	65	9/5/2017 19:56	64	11/5/2017 21:01	64
3/5/2017 19:41	63	5/5/2017 20:46	63	7/5/2017 9:51	63	7/5/2017 18:56	64	9/5/2017 20:01	64	11/5/2017 21:06	63
3/5/2017 19:46	65	5/5/2017 20:51	63	7/5/2017 9:56	63	7/5/2017 19:01	64	9/5/2017 20:06	64	11/5/2017 21:11	63
3/5/2017 19:51	63	5/5/2017 20:56	63	7/5/2017 10:01	63	7/5/2017 19:06	64	9/5/2017 20:11	64	11/5/2017 21:16	63
3/5/2017 19:56	63	5/5/2017 21:01	63	7/5/2017 10:06	64	7/5/2017 19:11	63	9/5/2017 20:16	64	11/5/2017 21:21	63
3/5/2017 20:01	63	5/5/2017 21:06	65	7/5/2017 10:11	64	7/5/2017 19:16	64	9/5/2017 20:21	63	11/5/2017 21:26	63
3/5/2017 20:06	62	5/5/2017 21:11	63	7/5/2017 10:16	65	7/5/2017 19:21	64	9/5/2017 20:26	63	11/5/2017 21:31	63
3/5/2017 20:11	62	5/5/2017 21:16	65	7/5/2017 10:21	64	7/5/2017 19:26	63	9/5/2017 20:31	63	11/5/2017 21:36	63
3/5/2017 20:16	62	5/5/2017 21:21	64	7/5/2017 10:26	64	7/5/2017 19:31	64	9/5/2017 20:36	63	11/5/2017 21:41	63
3/5/2017 20:21	63	5/5/2017 21:26	65	7/5/2017 10:31	64	7/5/2017 19:36	64	9/5/2017 20:41	62	11/5/2017 21:46	62
3/5/2017 20:26	62	5/5/2017 21:31	63	7/5/2017 10:36	66	7/5/2017 19:41	64	9/5/2017 20:46	62	11/5/2017 21:51	63
3/5/2017 20:31	62	5/5/2017 21:36	63	7/5/2017 10:41	66	7/5/2017 19:46	63	9/5/2017 20:51	63	11/5/2017 21:56	63
3/5/2017 20:36	62	5/5/2017 21:41	63	7/5/2017 10:46	67	7/5/2017 19:51	64	9/5/2017 20:56	63	11/5/2017 22:01	63
3/5/2017 20:41	62	5/5/2017 21:46	63	7/5/2017 10:51	66	7/5/2017 19:56	63	9/5/2017 21:01	63	11/5/2017 22:06	63
3/5/2017 20:46	62	5/5/2017 21:51	63	7/5/2017 10:56	65	7/5/2017 20:01	63	9/5/2017 21:06	63	11/5/2017 22:11	63
3/5/2017 20:51	62	5/5/2017 21:56	63	7/5/2017 11:01	65	7/5/2017 20:06	63	9/5/2017 21:11	63	11/5/2017 22:16	63
3/5/2017 20:56	62	5/5/2017 22:01	63	7/5/2017 11:06	64	7/5/2017 20:11	63	9/5/2017 21:16	63	11/5/2017 22:21	64
3/5/2017 21:01	63	5/5/2017 22:06	62	7/5/2017 11:11	67	7/5/2017 20:16	64	9/5/2017 21:21	63	11/5/2017 22:26	63
3/5/2017 21:06	62	5/5/2017 22:11	63	7/5/2017 11:16	64	7/5/2017 20:21	63	9/5/2017 21:26	63	11/5/2017 22:31	63
3/5/2017 21:11	62	5/5/2017 22:16	63	7/5/2017 11:21	65	7/5/2017 20:26	63	9/5/2017 21:31	63	11/5/2017 22:36	64
3/5/2017 21:16	62	5/5/2017 22:21	64	7/5/2017 11:26	65	7/5/2017 20:31	63	9/5/2017 21:36	63	11/5/2017 22:41	63
3/5/2017 21:21	62	5/5/2017 22:26	66	7/5/2017 11:31	65	7/5/2017 20:36	64	9/5/2017 21:41	65	11/5/2017 22:46	63
3/5/2017 21:26	62	5/5/2017 22:31	63	7/5/2017 11:36	65	7/5/2017 20:41	63	9/5/2017 21:46	63	11/5/2017 22:51	63
3/5/2017 21:31	62	5/5/2017 22:36	64	7/5/2017 11:41	65	7/5/2017 20:46	62	9/5/2017 21:51	64	11/5/2017 22:56	63
3/5/2017 21:36	62	5/5/2017 22:41	63	7/5/2017 11:46	65	7/5/2017 20:51	63	9/5/2017 21:56	64	12/5/2017 19:01	66
3/5/2017 21:41	62	5/5/2017 22:46	63	7/5/2017 11:51	64	7/5/2017 20:56	63	9/5/2017 22:01	63	12/5/2017 19:06	66
3/5/2017 21:46	62	5/5/2017 22:51	63	7/5/2017 11:56	64	7/5/2017 21:01	62	9/5/2017 22:06	63	12/5/2017 19:11	66
3/5/2017 21:51	62	5/5/2017 22:56	63	7/5/2017 12:01	64	7/5/2017 21:06	63	9/5/2017 22:11	63	12/5/2017 19:16	65
3/5/2017 21:56	62	6/5/2017 19:01	64	7/5/2017 12:06	63	7/5/2017 21:11	63	9/5/2017 22:16	63	12/5/2017 19:21	65
3/5/2017 22:01	62	6/5/2017 19:06	63	7/5/2017 12:11	65	7/5/2017 21:16	64	9/5/2017 22:21	63	12/5/2017 19:26	65
3/5/2017 22:06	62	6/5/2017 19:11	64	7/5/2017 12:16	66	7/5/2017 21:21	63	9/5/2017 22:26	63	12/5/2017 19:31	65
3/5/2017 22:11	62	6/5/2017 19:16	63	7/5/2017 12:21	65	7/5/2017 21:26	63	9/5/2017 22:31	63	12/5/2017 19:36	63
3/5/2017 22:16	65	6/5/2017 19:21	64	7/5/2017 12:26	64	7/5/2017 21:31	63	9/5/2017 22:36	64	12/5/2017 19:41	63
3/5/2017 22:21	62	6/5/2017 19:26	64	7/5/2017 12:31	64	7/5/2017 21:36	63	9/5/2017 22:41	63	12/5/2017 19:46	63
3/5/2017 22:26	63	6/5/2017 19:31	64	7/5/2017 12:36	64	7/5/2017 21:41	63	9/5/2017 22:46	65	12/5/2017 19:51	63
3/5/2017 22:31	62	6/5/2017 19:36	64	7/5/2017 12:41	65	7/5/2017 21:46	63	9/5/2017 22:51	63	12/5/2017 19:56	63
3/5/2017 22:36	61	6/5/2017 19:41	63	7/5/2017 12:46	65	7/5/2017 21:51	63	9/5/2017 22:56	62	12/5/2017 20:01	62
3/5/2017 22:41	62	6/5/2017 19:46	63	7/5/2017 12:51	65	7/5/2017 21:56	63	10/5/2017 19:01	65	12/5/2017 20:06	63
3/5/2017 22:46	61	6/5/2017 19:51	63	7/5/2017 12:56	65	7/5/2017 22:01	63	10/5/2017 19:06	65	12/5/2017 20:11	64
3/5/2017 22:51	65	6/5/2017 19:56	64	7/5/2017 13:01	64	7/5/2017 22:06	62	10/5/2017 19:11	66	12/5/2017 20:16	64
3/5/2017 22:56	61	6/5/2017 20:01	64	7/5/2017 13:06	64	7/5/2017 22:11	62	10/5/2017 19:16	65	12/5/2017 20:21	64
4/5/2017 19:01	67	6/5/2017 20:06	63	7/5/2017 13:11	64	7/5/2017 22:16	63	10/5/2017 19:21	65	12/5/2017 20:26	64
4/5/2017 19:06	66	6/5/2017 20:11	64	7/5/2017 13:16	64	7/5/2017 22:21	63	10/5/2017 19:26	65	12/5/2017 20:31	64
4/5/2017 19:11	66	6/5/2017 20:16	62	7/5/2017 13:21	65	7/5/2017 22:26	63	10/5/2017 19:31	64	12/5/2017 20:36	63
4/5/2017 19:16	66	6/5/2017 20:21	62	7/5/2017 13:26	65	7/5/2017 22:31	63	10/5/2017 19:36	63	12/5/2017 20:41	64
4/5/2017 19:21	66	6/5/2017 20:26	63	7/5/2017 13:31	64	7/5/2017 22:36	63	10/5/2017 19:41	62	12/5/2017 20:46	63
4/5/2017 19:26	66	6/5/2017 20:31	63	7/5/2017 13:36	63	7/5/2017 22:41	62	10/5/2017 19:46	63	12/5/2017 20:51	63
4/5/2017 19:31	65	6/5/2017 20:36	63	7/5/2017 13:41	65	7/5/2017 22:46	63	10/5/2017 19:51	63	12/5/2017 20:56	63
4/5/2017 19:36	65	6/5/2017 20:41	62	7/5/2017 13:46	64	7/5/2017 22:51	63	10/5/2017 19:56	64	12/5/2017 21:01	63
4/5/2017 19:41	64	6/5/2017 20:46	63	7/5/2017 13:51	65	7/5/2017 22:56	62	10/5/2017 20:01	63	12/5/2017 21:06	63
4/5/2017 19:46	64	6/5/2017 20:51	62	7/5/2017 13:56	65	8/5/2017 19:01	67	10/5/2017 20:06	64	12/5/2017 21:11	63
4/5/2017 19:51	64	6/5/2017 20:56	63	7/5/2017 14:01	64	8/5/2017 19:06	67	10/5/2017 20:11	63	12/5/2017 21:16	63
4/5/2017 19:56	64	6/5/2017 21:01	63	7/5/2017 14:06	65	8/5/2017 19:11	67	10/5/2017 20:16	64	12/5/2017 21:21	63
4/5/2017 20:01	64	6/5/2017 21:06	63	7/5/2017 14:11	65	8/5/2017 19:16	65	10/5/2017 20:21	64	12/5/2017 21:26	62
4/5/2017 20:06	64	6/5/2017 21:11	64	7/5/2017 14:16	64	8/5/2017 19:21	66	10/5/2017 20:26	64	12/5/2017 21:31	63
4/5/2017 20:11	64	6/5/2017 21:16	63	7/5/2017 14:21	65	8/5/2017 19:26	65	10/5/2017 20:31	63	12/5/2017 21:36	63
4/5/2017 20:16	65	6/5/2017 21:21	62	7/5/2017 14:26	64	8/5/2017 19:31	64	10/5/2017 20:36	64	12/5/2017 21:41	63
4/5/2017 20:21	64	6/5/2017 21:26	62	7/5/2017 14:31	64	8/5/2017 19:36	64	10/5/2017 20:41	63	12/5/2017 21:46	63
4/5/2017 20:26	64	6/5/2017 21:31	63	7/5/2017 14:36	65	8/5/2017 19:41	64	10/5/2017 20:46	64	12/5/2017 21:51	63
4/5/2017 20:31	64	6/5/2017 21:36	63	7/5/2017 14:41	65	8/5/2017 19:46	64	10/5/2017 20:51	63	12/5/2017 21:56	63
4/5/2017 20:36	64	6/5/2017 21:41	63	7/5/2017 14:46	64	8/5/2017 19:51	64	10/5/2017 20:56	63	12/5/2017 22:01	63
4/5/2017 20:41	64	6/5/2017 21:46	63	7/5/2017 14:51	64	8/5/2017 19:56	64	10/5/2017 21:01	63	12/5/2017 22:06	63
4/5/2017 20:46	64	6/5/2017 21:51	63	7/5/2017 14:56	64	8/5/2017 20:01	64	10/5/2017 21:06	63	12/5/2017 22:11	63
4/5/2017 20:51	63	6/5/2017 21:56	65	7/5/2017 15:01	65	8/5/2017 20:06	64	10/5/2017 21:11	63	12/5/2017 22:16	64
4/5/2017 20:56	64	6/5/2017 22:01	64	7/5/2017 15:06	64	8/5/2017 20:11	64	10/5/2017 21:16	63	12/5/2017 22:21	64
4/5/2017 21:01	64	6/5/2017 22:06	63	7/5/2017 15:11	64	8/5/2017 20:16	64	10/5/2017 21:21	64	12/5/2017 22:26	64
4/5/2017 21:06	63	6/5/2017 22:11	63	7/5/2017 15:16	64	8/5/2017 20:21	64	10/5/2017 21:26	63	12/5/2017 22:31	63
4/5/2017 21:11	63	6/5/2017 22:16	64	7/5/2017 15:21	64	8/5/2017 20:26	64	10/5/2017 21:31	63	12/5/2017 22:36	65
4/5/2017 21:16	63	6/5/2017 22:21	63	7/5/2017 15:26	64	8/5/2017 20:31	64	10/5/2017 21:36	62	12/5/2017 22:41	65
4/5/2017 21:21	64	6/5/2017 22:26	63	7/5/2017 15:31	64	8/5/2017 20:36	64	10/5/2017 21:41	63	12/5/2017 22:46	63
4/5/2017 21:26	64	6/5/2017 22:31	63	7/5/2017 15:36	64	8/5/2017 20:41	63	10/5/2017 21:46	63	12/5/2017 22:51	63
4/5/2017 21:31	63	6/5/2017 22:36	63	7/5/2017 15:41	65	8/5/2017 20:46	63	10/5/2017 21:51	64	12/5/2017 22:56	64
4/5/2017 21:36	64	6/5/2017 22:41	63	7/5/2017 15:46	64	8/5/2017 20:51	64	10/5/2017 21:56	64	13/5/2017 19:01	65
4/5/2017 21:41	64	6/5/2017 22:46	62	7/5/2017 15:51	65	8/5/2017 20:56	63	10/5/2017 22:01	64	13/5/2017 19:06	64
4/5/2017 21:46	63	6/5/2017 22									

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
13/5/2017 22:01	62	14/5/2017 15:06	65	15/5/2017 20:11	64	17/5/2017 21:16	63	19/5/2017 22:21	64	21/5/2017 11:26	64
13/5/2017 22:06	63	14/5/2017 15:11	65	15/5/2017 20:16	64	17/5/2017 21:21	62	19/5/2017 22:26	64	21/5/2017 11:31	64
13/5/2017 22:11	63	14/5/2017 15:16	65	15/5/2017 20:21	64	17/5/2017 21:26	63	19/5/2017 22:31	64	21/5/2017 11:36	63
13/5/2017 22:16	63	14/5/2017 15:21	65	15/5/2017 20:26	64	17/5/2017 21:31	63	19/5/2017 22:36	64	21/5/2017 11:41	66
13/5/2017 22:21	64	14/5/2017 15:26	65	15/5/2017 20:31	64	17/5/2017 21:36	63	19/5/2017 22:41	64	21/5/2017 11:46	64
13/5/2017 22:26	63	14/5/2017 15:31	65	15/5/2017 20:36	65	17/5/2017 21:41	64	19/5/2017 22:46	64	21/5/2017 11:51	65
13/5/2017 22:31	64	14/5/2017 15:36	64	15/5/2017 20:41	64	17/5/2017 21:46	63	19/5/2017 22:51	63	21/5/2017 11:56	64
13/5/2017 22:36	64	14/5/2017 15:41	65	15/5/2017 20:46	64	17/5/2017 21:51	63	19/5/2017 22:56	63	21/5/2017 12:01	64
13/5/2017 22:41	64	14/5/2017 15:46	64	15/5/2017 20:51	64	17/5/2017 21:56	63	20/5/2017 19:01	64	21/5/2017 12:06	65
13/5/2017 22:46	64	14/5/2017 15:51	65	15/5/2017 20:56	64	17/5/2017 22:01	63	20/5/2017 19:06	63	21/5/2017 12:11	64
13/5/2017 22:51	64	14/5/2017 15:56	67	15/5/2017 21:01	63	17/5/2017 22:06	64	20/5/2017 19:11	64	21/5/2017 12:16	64
13/5/2017 22:56	64	14/5/2017 16:01	67	15/5/2017 21:06	64	17/5/2017 22:11	63	20/5/2017 19:16	63	21/5/2017 12:21	66
14/5/2017 7:01	61	14/5/2017 16:06	67	15/5/2017 21:11	64	17/5/2017 22:16	64	20/5/2017 19:21	64	21/5/2017 12:26	65
14/5/2017 7:06	61	14/5/2017 16:11	66	15/5/2017 21:16	64	17/5/2017 22:21	63	20/5/2017 19:26	64	21/5/2017 12:31	65
14/5/2017 7:11	63	14/5/2017 16:16	67	15/5/2017 21:21	64	17/5/2017 22:26	63	20/5/2017 19:31	64	21/5/2017 12:36	64
14/5/2017 7:16	62	14/5/2017 16:21	67	15/5/2017 21:26	64	17/5/2017 22:31	64	20/5/2017 19:36	63	21/5/2017 12:41	65
14/5/2017 7:21	62	14/5/2017 16:26	66	15/5/2017 21:31	64	17/5/2017 22:36	64	20/5/2017 19:41	64	21/5/2017 12:46	66
14/5/2017 7:26	61	14/5/2017 16:31	67	15/5/2017 21:36	66	17/5/2017 22:41	63	20/5/2017 19:46	64	21/5/2017 12:51	66
14/5/2017 7:31	61	14/5/2017 16:36	67	15/5/2017 21:41	64	17/5/2017 22:46	63	20/5/2017 19:51	63	21/5/2017 12:56	66
14/5/2017 7:36	62	14/5/2017 16:41	67	15/5/2017 21:46	64	17/5/2017 22:51	63	20/5/2017 19:56	63	21/5/2017 13:01	66
14/5/2017 7:41	64	14/5/2017 16:46	67	15/5/2017 21:51	64	17/5/2017 22:56	63	20/5/2017 20:01	65	21/5/2017 13:06	66
14/5/2017 7:46	62	14/5/2017 16:51	66	15/5/2017 21:56	64	18/5/2017 19:01	64	20/5/2017 20:06	64	21/5/2017 13:11	65
14/5/2017 7:51	65	14/5/2017 16:56	65	15/5/2017 22:01	64	18/5/2017 19:06	64	20/5/2017 20:11	64	21/5/2017 13:16	67
14/5/2017 7:56	63	14/5/2017 17:01	65	15/5/2017 22:06	64	18/5/2017 19:11	64	20/5/2017 20:16	63	21/5/2017 13:21	67
14/5/2017 8:01	63	14/5/2017 17:06	65	15/5/2017 22:11	66	18/5/2017 19:16	64	20/5/2017 20:21	63	21/5/2017 13:26	65
14/5/2017 8:06	63	14/5/2017 17:11	65	15/5/2017 22:16	64	18/5/2017 19:21	64	20/5/2017 20:26	64	21/5/2017 13:31	64
14/5/2017 8:11	62	14/5/2017 17:16	64	15/5/2017 22:21	64	18/5/2017 19:26	65	20/5/2017 20:31	63	21/5/2017 13:36	66
14/5/2017 8:16	63	14/5/2017 17:21	64	15/5/2017 22:26	63	18/5/2017 19:31	65	20/5/2017 20:36	63	21/5/2017 13:41	68
14/5/2017 8:21	63	14/5/2017 17:26	65	15/5/2017 22:31	63	18/5/2017 19:36	64	20/5/2017 20:41	63	21/5/2017 13:46	69
14/5/2017 8:26	62	14/5/2017 17:31	65	15/5/2017 22:36	64	18/5/2017 19:41	64	20/5/2017 20:46	63	21/5/2017 13:51	67
14/5/2017 8:31	63	14/5/2017 17:36	65	15/5/2017 22:41	63	18/5/2017 19:46	65	20/5/2017 20:51	63	21/5/2017 13:56	66
14/5/2017 8:36	63	14/5/2017 17:41	65	15/5/2017 22:46	64	18/5/2017 19:51	64	20/5/2017 20:56	63	21/5/2017 14:01	66
14/5/2017 8:41	62	14/5/2017 17:46	65	15/5/2017 22:51	64	18/5/2017 19:56	64	20/5/2017 21:01	63	21/5/2017 14:06	66
14/5/2017 8:46	63	14/5/2017 17:51	64	15/5/2017 22:56	64	18/5/2017 20:01	63	20/5/2017 21:06	62	21/5/2017 14:11	67
14/5/2017 8:51	63	14/5/2017 17:56	64	16/5/2017 19:01	65	18/5/2017 20:06	64	20/5/2017 21:11	63	21/5/2017 14:16	67
14/5/2017 8:56	62	14/5/2017 18:01	64	16/5/2017 19:06	66	18/5/2017 20:11	64	20/5/2017 21:16	62	21/5/2017 14:21	66
14/5/2017 9:01	62	14/5/2017 18:06	65	16/5/2017 19:11	66	18/5/2017 20:16	64	20/5/2017 21:21	62	21/5/2017 14:26	66
14/5/2017 9:06	63	14/5/2017 18:11	64	16/5/2017 19:16	66	18/5/2017 20:21	63	20/5/2017 21:26	64	21/5/2017 14:31	65
14/5/2017 9:11	64	14/5/2017 18:16	64	16/5/2017 19:21	67	18/5/2017 20:26	63	20/5/2017 21:31	62	21/5/2017 14:36	66
14/5/2017 9:16	63	14/5/2017 18:21	64	16/5/2017 19:26	66	18/5/2017 20:31	63	20/5/2017 21:36	65	21/5/2017 14:41	65
14/5/2017 9:21	63	14/5/2017 18:26	64	16/5/2017 19:31	65	18/5/2017 20:36	64	20/5/2017 21:41	63	21/5/2017 14:46	66
14/5/2017 9:26	64	14/5/2017 18:31	63	16/5/2017 19:36	64	18/5/2017 20:41	63	20/5/2017 21:46	62	21/5/2017 14:51	66
14/5/2017 9:31	64	14/5/2017 18:36	64	16/5/2017 19:41	64	18/5/2017 20:46	63	20/5/2017 21:51	65	21/5/2017 14:56	66
14/5/2017 9:36	64	14/5/2017 18:41	64	16/5/2017 19:46	64	18/5/2017 20:51	63	20/5/2017 21:56	62	21/5/2017 15:01	66
14/5/2017 9:41	64	14/5/2017 18:46	64	16/5/2017 19:51	64	18/5/2017 20:56	63	20/5/2017 22:01	63	21/5/2017 15:06	66
14/5/2017 9:46	63	14/5/2017 18:51	64	16/5/2017 19:56	64	18/5/2017 21:01	63	20/5/2017 22:06	63	21/5/2017 15:11	65
14/5/2017 9:51	64	14/5/2017 18:56	64	16/5/2017 20:01	65	18/5/2017 21:06	63	20/5/2017 22:11	63	21/5/2017 15:16	65
14/5/2017 9:56	63	14/5/2017 19:01	64	16/5/2017 20:06	64	18/5/2017 21:11	63	20/5/2017 22:16	63	21/5/2017 15:21	66
14/5/2017 10:01	64	14/5/2017 19:06	65	16/5/2017 20:11	64	18/5/2017 21:16	64	20/5/2017 22:21	63	21/5/2017 15:26	65
14/5/2017 10:06	64	14/5/2017 19:11	65	16/5/2017 20:16	64	18/5/2017 21:21	63	20/5/2017 22:26	62	21/5/2017 15:31	65
14/5/2017 10:11	65	14/5/2017 19:16	64	16/5/2017 20:21	65	18/5/2017 21:26	63	20/5/2017 22:31	62	21/5/2017 15:36	65
14/5/2017 10:16	64	14/5/2017 19:21	64	16/5/2017 20:26	64	18/5/2017 21:31	63	20/5/2017 22:36	63	21/5/2017 15:41	65
14/5/2017 10:21	64	14/5/2017 19:26	64	16/5/2017 20:31	64	18/5/2017 21:36	63	20/5/2017 22:41	63	21/5/2017 15:46	65
14/5/2017 10:26	64	14/5/2017 19:31	63	16/5/2017 20:36	64	18/5/2017 21:41	64	20/5/2017 22:46	63	21/5/2017 15:51	67
14/5/2017 10:31	64	14/5/2017 19:36	64	16/5/2017 20:41	63	18/5/2017 21:46	63	20/5/2017 22:51	63	21/5/2017 15:56	65
14/5/2017 10:36	65	14/5/2017 19:41	64	16/5/2017 20:46	64	18/5/2017 21:51	63	20/5/2017 22:56	62	21/5/2017 16:01	65
14/5/2017 10:41	64	14/5/2017 19:46	64	16/5/2017 20:51	64	18/5/2017 21:56	64	21/5/2017 7:01	62	21/5/2017 16:06	65
14/5/2017 10:46	64	14/5/2017 19:51	63	16/5/2017 20:56	64	18/5/2017 22:01	64	21/5/2017 7:06	62	21/5/2017 16:11	65
14/5/2017 10:51	64	14/5/2017 19:56	63	16/5/2017 21:01	63	18/5/2017 22:06	63	21/5/2017 7:11	65	21/5/2017 16:16	66
14/5/2017 10:56	65	14/5/2017 20:01	63	16/5/2017 21:06	63	18/5/2017 22:11	63	21/5/2017 7:16	63	21/5/2017 16:21	65
14/5/2017 11:01	65	14/5/2017 20:06	63	16/5/2017 21:11	64	18/5/2017 22:16	64	21/5/2017 7:21	64	21/5/2017 16:26	65
14/5/2017 11:06	63	14/5/2017 20:11	63	16/5/2017 21:16	64	18/5/2017 22:21	63	21/5/2017 7:26	63	21/5/2017 16:31	66
14/5/2017 11:11	63	14/5/2017 20:16	63	16/5/2017 21:21	63	18/5/2017 22:26	63	21/5/2017 7:31	62	21/5/2017 16:36	65
14/5/2017 11:16	64	14/5/2017 20:21	63	16/5/2017 21:26	63	18/5/2017 22:31	63	21/5/2017 7:36	63	21/5/2017 16:41	66
14/5/2017 11:21	64	14/5/2017 20:26	63	16/5/2017 21:31	63	18/5/2017 22:36	63	21/5/2017 7:41	63	21/5/2017 16:46	65
14/5/2017 11:26	64	14/5/2017 20:31	63	16/5/2017 21:36	63	18/5/2017 22:41	63	21/5/2017 7:46	63	21/5/2017 16:51	66
14/5/2017 11:31	63	14/5/2017 20:36	63	16/5/2017 21:41	63	18/5/2017 22:46	63	21/5/2017 7:51	63	21/5/2017 16:56	68
14/5/2017 11:36	64	14/5/2017 20:41	65	16/5/2017 21:46	64	18/5/2017 22:51	63	21/5/2017 7:56	63	21/5/2017 17:01	67
14/5/2017 11:41	64	14/5/2017 20:46	63	16/5/2017 21:51	64	18/5/2017 22:56	63	21/5/2017 8:01	63	21/5/2017 17:06	67
14/5/2017 11:46	64	14/5/2017 20:51	63	16/5/2017 21:56	64	19/5/2017 19:01	66	21/5/2017 8:06	63	21/5/2017 17:11	68
14/5/2017 11:51	64	14/5/2017 20:56	63	16/5/2017 22:01	63	19/5/2017 19:06	67	21/5/2017 8:11	63	21/5/2017 17:16	67
14/5/2017 11:56	64	14/5/2017 21:01	63	16/5/2017 22:06	63	19/5/2017 19:11	66	21/5/2017 8:16	64	21/5/2017 17:21	69
14/5/2017 12:01	64	14/5/2017 21:06	63	16/5/2017 22:11	65	19/5/2017 19:16	66	21/5/2017 8:21	63	21/5/2017 17:26	67
14/5/2017 12:06	64	14/5/2017 21:11	63	16/5/2017 22:16	63	1					

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
21/5/2017 20:31	66	23/5/2017 21:36	63	25/5/2017 22:41	64	27/4/2017 4:31	58	28/4/2017 5:36	59	29/4/2017 6:41	62
21/5/2017 20:36	65	23/5/2017 21:41	64	25/5/2017 22:46	64	27/4/2017 4:36	58	28/4/2017 5:41	60	29/4/2017 6:46	57
21/5/2017 20:41	64	23/5/2017 21:46	64	25/5/2017 22:51	64	27/4/2017 4:41	58	28/4/2017 5:46	61	29/4/2017 6:51	59
21/5/2017 20:46	64	23/5/2017 21:51	64	25/5/2017 22:56	63	27/4/2017 4:46	59	28/4/2017 5:51	60	29/4/2017 6:56	57
21/5/2017 20:51	64	23/5/2017 21:56	65	26/5/2017 19:01	65	27/4/2017 4:51	59	28/4/2017 5:56	61	29/4/2017 7:01	56
21/5/2017 20:56	64	23/5/2017 22:01	64	26/5/2017 19:06	65	27/4/2017 4:56	58	28/4/2017 6:01	61	29/4/2017 7:06	53
21/5/2017 21:01	64	23/5/2017 22:06	63	26/5/2017 19:11	66	27/4/2017 5:01	59	28/4/2017 6:06	61	29/4/2017 7:11	56
21/5/2017 21:06	64	23/5/2017 22:11	64	26/5/2017 19:16	65	27/4/2017 5:06	59	28/4/2017 6:11	61	29/4/2017 7:16	55
21/5/2017 21:11	64	23/5/2017 22:16	63	26/5/2017 19:21	66	27/4/2017 5:11	58	28/4/2017 6:16	51	29/4/2017 7:21	53
21/5/2017 21:16	64	23/5/2017 22:21	63	26/5/2017 19:26	65	27/4/2017 5:16	59	28/4/2017 6:21	62	29/4/2017 7:26	51
21/5/2017 21:21	64	23/5/2017 22:26	63	26/5/2017 19:31	64	27/4/2017 5:21	59	28/4/2017 6:26	57	29/4/2017 7:31	62
21/5/2017 21:26	64	23/5/2017 22:31	64	26/5/2017 19:36	64	27/4/2017 5:26	59	28/4/2017 6:31	51	29/4/2017 7:36	48
21/5/2017 21:31	64	23/5/2017 22:36	64	26/5/2017 19:41	62	27/4/2017 5:31	60	28/4/2017 6:36	59	29/4/2017 7:41	62
21/5/2017 21:36	64	23/5/2017 22:41	63	26/5/2017 19:46	62	27/4/2017 5:36	59	28/4/2017 6:41	61	29/4/2017 7:46	48
21/5/2017 21:41	64	23/5/2017 22:46	63	26/5/2017 19:51	62	27/4/2017 5:41	60	28/4/2017 6:46	60	29/4/2017 7:51	57
21/5/2017 21:46	64	23/5/2017 22:51	64	26/5/2017 19:56	62	27/4/2017 5:46	61	28/4/2017 6:51	60	29/4/2017 7:56	44
21/5/2017 21:51	64	23/5/2017 22:56	63	26/5/2017 20:01	62	27/4/2017 5:51	60	28/4/2017 6:56	60	30/4/2017 0:01	62
21/5/2017 21:56	64	24/5/2017 19:01	66	26/5/2017 20:06	63	27/4/2017 5:56	60	28/4/2017 7:01	58	30/4/2017 0:06	46
21/5/2017 22:01	64	24/5/2017 19:06	66	26/5/2017 20:11	62	27/4/2017 6:01	61	28/4/2017 7:06	57	30/4/2017 0:11	61
21/5/2017 22:06	64	24/5/2017 19:11	66	26/5/2017 20:16	62	27/4/2017 6:06	62	28/4/2017 7:11	58	30/4/2017 0:16	44
21/5/2017 22:11	64	24/5/2017 19:16	66	26/5/2017 20:21	63	27/4/2017 6:11	62	28/4/2017 7:16	57	30/4/2017 0:21	61
21/5/2017 22:16	64	24/5/2017 19:21	66	26/5/2017 20:26	62	27/4/2017 6:16	50	28/4/2017 7:21	59	30/4/2017 0:26	62
21/5/2017 22:21	64	24/5/2017 19:26	66	26/5/2017 20:31	62	27/4/2017 6:21	56	28/4/2017 7:26	57	30/4/2017 0:31	61
21/5/2017 22:26	64	24/5/2017 19:31	66	26/5/2017 20:36	63	27/4/2017 6:26	58	28/4/2017 7:31	58	30/4/2017 0:36	61
21/5/2017 22:31	63	24/5/2017 19:36	65	26/5/2017 20:41	63	27/4/2017 6:31	60	28/4/2017 7:36	57	30/4/2017 0:41	61
21/5/2017 22:36	64	24/5/2017 19:41	65	26/5/2017 20:46	62	27/4/2017 6:36	61	28/4/2017 7:41	59	30/4/2017 0:46	61
21/5/2017 22:41	64	24/5/2017 19:46	67	26/5/2017 20:51	63	27/4/2017 6:41	60	28/4/2017 7:46	55	30/4/2017 0:51	61
21/5/2017 22:46	64	24/5/2017 19:51	66	26/5/2017 20:56	63	27/4/2017 6:46	61	28/4/2017 7:51	54	30/4/2017 0:56	42
21/5/2017 22:51	63	24/5/2017 19:56	65	26/5/2017 21:01	62	27/4/2017 6:51	61	28/4/2017 7:56	56	30/4/2017 1:01	61
21/5/2017 22:56	62	24/5/2017 20:01	66	26/5/2017 21:06	62	27/4/2017 6:56	61	29/4/2017 0:01	55	30/4/2017 1:06	61
22/5/2017 19:01	66	24/5/2017 20:06	64	26/5/2017 21:11	62	27/4/2017 7:01	59	29/4/2017 0:06	55	30/4/2017 1:11	61
22/5/2017 19:06	67	24/5/2017 20:11	65	26/5/2017 21:16	63	27/4/2017 7:06	57	29/4/2017 0:11	60	30/4/2017 1:16	61
22/5/2017 19:11	66	24/5/2017 20:16	65	26/5/2017 21:21	63	27/4/2017 7:11	59	29/4/2017 0:16	56	30/4/2017 1:21	61
22/5/2017 19:16	66	24/5/2017 20:21	64	26/5/2017 21:26	64	27/4/2017 7:16	58	29/4/2017 0:21	46	30/4/2017 1:26	61
22/5/2017 19:21	66	24/5/2017 20:26	64	26/5/2017 21:31	63	27/4/2017 7:21	57	29/4/2017 0:26	45	30/4/2017 1:31	61
22/5/2017 19:26	66	24/5/2017 20:31	65	26/5/2017 21:36	63	27/4/2017 7:26	58	29/4/2017 0:31	54	30/4/2017 1:36	60
22/5/2017 19:31	65	24/5/2017 20:36	65	26/5/2017 21:41	63	27/4/2017 7:31	51	29/4/2017 0:36	62	30/4/2017 1:41	60
22/5/2017 19:36	65	24/5/2017 20:41	66	26/5/2017 21:46	62	27/4/2017 7:36	54	29/4/2017 0:41	49	30/4/2017 1:46	60
22/5/2017 19:41	65	24/5/2017 20:46	64	26/5/2017 21:51	65	27/4/2017 7:41	54	29/4/2017 0:46	56	30/4/2017 1:51	60
22/5/2017 19:46	65	24/5/2017 20:51	64	26/5/2017 21:56	65	27/4/2017 7:46	48	29/4/2017 0:51	61	30/4/2017 1:56	60
22/5/2017 19:51	64	24/5/2017 20:56	65	26/5/2017 22:01	64	27/4/2017 7:51	51	29/4/2017 0:56	61	30/4/2017 2:01	63
22/5/2017 19:56	65	24/5/2017 21:01	65	26/5/2017 22:06	65	27/4/2017 7:56	58	29/4/2017 1:01	61	30/4/2017 2:06	60
22/5/2017 20:01	65	24/5/2017 21:06	64	26/5/2017 22:11	65	28/4/2017 0:01	53	29/4/2017 1:06	62	30/4/2017 2:11	60
22/5/2017 20:06	64	24/5/2017 21:11	64	26/5/2017 22:16	64	28/4/2017 0:06	52	29/4/2017 1:11	61	30/4/2017 2:16	60
22/5/2017 20:11	64	24/5/2017 21:16	64	26/5/2017 22:21	63	28/4/2017 0:11	43	29/4/2017 1:16	62	30/4/2017 2:21	60
22/5/2017 20:16	64	24/5/2017 21:21	64	26/5/2017 22:26	64	28/4/2017 0:16	50	29/4/2017 1:21	62	30/4/2017 2:26	60
22/5/2017 20:21	64	24/5/2017 21:26	65	26/5/2017 22:31	63	28/4/2017 0:21	62	29/4/2017 1:26	61	30/4/2017 2:31	60
22/5/2017 20:26	64	24/5/2017 21:31	64	26/5/2017 22:36	63	28/4/2017 0:26	49	29/4/2017 1:31	61	30/4/2017 2:36	59
22/5/2017 20:31	64	24/5/2017 21:36	65	26/5/2017 22:41	63	28/4/2017 0:31	62	29/4/2017 1:36	61	30/4/2017 2:41	60
22/5/2017 20:36	63	24/5/2017 21:41	64	26/5/2017 22:46	64	28/4/2017 0:36	61	29/4/2017 1:41	61	30/4/2017 2:46	60
22/5/2017 20:41	64	24/5/2017 21:46	64	26/5/2017 22:51	64	28/4/2017 0:41	62	29/4/2017 1:46	61	30/4/2017 2:51	59
22/5/2017 20:46	64	24/5/2017 21:51	64	26/5/2017 22:56	63	28/4/2017 0:46	61	29/4/2017 1:51	61	30/4/2017 2:56	60
22/5/2017 20:51	64	24/5/2017 21:56	64	Night time: 23:00-07:00							
22/5/2017 20:56	64	24/5/2017 22:01	63	27/4/2017 0:01	62	28/4/2017 0:51	61	29/4/2017 1:56	60	30/4/2017 3:01	60
22/5/2017 21:01	64	24/5/2017 22:06	63	27/4/2017 0:06	62	28/4/2017 0:56	61	29/4/2017 2:01	61	30/4/2017 3:06	59
22/5/2017 21:06	64	24/5/2017 22:11	64	27/4/2017 0:11	54	28/4/2017 1:01	61	29/4/2017 2:06	61	30/4/2017 3:11	59
22/5/2017 21:11	64	24/5/2017 22:16	64	27/4/2017 0:16	62	28/4/2017 1:06	61	29/4/2017 2:11	60	30/4/2017 3:16	60
22/5/2017 21:16	64	24/5/2017 22:21	63	27/4/2017 0:21	61	28/4/2017 1:11	60	29/4/2017 2:16	61	30/4/2017 3:21	59
22/5/2017 21:21	63	24/5/2017 22:26	64	27/4/2017 0:26	62	28/4/2017 1:16	61	29/4/2017 2:21	61	30/4/2017 3:26	59
22/5/2017 21:26	63	24/5/2017 22:31	64	27/4/2017 0:31	62	28/4/2017 1:21	60	29/4/2017 2:26	60	30/4/2017 3:31	60
22/5/2017 21:31	63	24/5/2017 22:36	64	27/4/2017 0:36	61	28/4/2017 1:26	60	29/4/2017 2:31	61	30/4/2017 3:36	59
22/5/2017 21:36	64	24/5/2017 22:41	64	27/4/2017 0:41	61	28/4/2017 1:31	61	29/4/2017 2:36	60	30/4/2017 3:41	59
22/5/2017 21:41	63	24/5/2017 22:46	63	27/4/2017 0:46	61	28/4/2017 1:36	60	29/4/2017 2:41	61	30/4/2017 3:46	60
22/5/2017 21:46	64	24/5/2017 22:51	64	27/4/2017 0:51	61	28/4/2017 1:41	59	29/4/2017 2:46	60	30/4/2017 3:51	59
22/5/2017 21:51	64	24/5/2017 22:56	63	27/4/2017 0:56	61	28/4/2017 1:46	60	29/4/2017 2:51	61	30/4/2017 3:56	60
22/5/2017 21:56	64	25/5/2017 19:01	66	27/4/2017 1:01	60	28/4/2017 1:51	60	29/4/2017 2:56	60	30/4/2017 4:01	58
22/5/2017 22:01	64	25/5/2017 19:06	66	27/4/2017 1:06	61	28/4/2017 1:56	60	29/4/2017 3:01	60	30/4/2017 4:06	59
22/5/2017 22:06	63	25/5/2017 19:11	67	27/4/2017 1:11	61	28/4/2017 2:01	59	29/4/2017 3:06	60	30/4/2017 4:11	57
22/5/2017 22:11	64	25/5/2017 19:16	66	27/4/2017 1:16	59	28/4/2017 2:06	59	29/4/2017 3:11	60	30/4/2017 4:16	58
22/5/2017 22:16	66	25/5/2017 19:21	66	27/4/2017 1:21	61	28/4/2017 2:11	59	29/4/2017 3:16	60	30/4/2017 4:21	58
22/5/2017 22:21	66	25/5/2017 19:26	66	27/4/2017 1:26	60	28/4/2017 2:16	59	29/4/2017 3:21	60	30/4/2017 4:26	58
22/5/2017 22:26	66	25/5/2017 19:31	66	27/4/2017 1:31	59	28/4/2017 2:21	59	29/4/2017 3:26	59	30/4/2017 4:31	59
22/5/2017 22:31	66	25/5/2017 19:36	65	27/4/2017 1:36	61	28/4/2017 2:26	60	29/4/2017 3:31	60	30/4/2017 4:36	58
22/5/2017 22:36	66	25/5/2017 19:41	65	27/4/2017 1:41	61	28/4/2017 2:31	59	29/4/2017 3:36	60	30/4/2017 4:41	59
22/5/2017 22:41	65	25/5/2017 19:46	65	27/4/2017 1:46	60	28/4/2017 2:36	58	29/4/2017 3:41			

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
30/4/2017 23:46	61	2/5/2017 0:51	60	3/5/2017 1:56	60	4/5/2017 3:01	58	5/5/2017 4:06	57	6/5/2017 5:11	59
30/4/2017 23:51	61	2/5/2017 0:56	60	3/5/2017 2:01	60	4/5/2017 3:06	56	5/5/2017 4:11	58	6/5/2017 5:16	58
30/4/2017 23:56	61	2/5/2017 1:01	59	3/5/2017 2:06	60	4/5/2017 3:11	57	5/5/2017 4:16	58	6/5/2017 5:21	60
1/5/2017 0:01	61	2/5/2017 1:06	58	3/5/2017 2:11	59	4/5/2017 3:16	57	5/5/2017 4:21	59	6/5/2017 5:26	59
1/5/2017 0:06	61	2/5/2017 1:11	58	3/5/2017 2:16	59	4/5/2017 3:21	57	5/5/2017 4:26	58	6/5/2017 5:31	59
1/5/2017 0:11	61	2/5/2017 1:16	60	3/5/2017 2:21	59	4/5/2017 3:26	58	5/5/2017 4:31	58	6/5/2017 5:36	59
1/5/2017 0:16	61	2/5/2017 1:21	59	3/5/2017 2:26	60	4/5/2017 3:31	57	5/5/2017 4:36	59	6/5/2017 5:41	60
1/5/2017 0:21	61	2/5/2017 1:26	58	3/5/2017 2:31	59	4/5/2017 3:36	57	5/5/2017 4:41	58	6/5/2017 5:46	60
1/5/2017 0:26	60	2/5/2017 1:31	59	3/5/2017 2:36	59	4/5/2017 3:41	57	5/5/2017 4:46	57	6/5/2017 5:51	60
1/5/2017 0:31	61	2/5/2017 1:36	61	3/5/2017 2:41	59	4/5/2017 3:46	57	5/5/2017 4:51	58	6/5/2017 5:56	61
1/5/2017 0:36	60	2/5/2017 1:41	58	3/5/2017 2:46	61	4/5/2017 3:51	56	5/5/2017 4:56	58	6/5/2017 6:01	60
1/5/2017 0:41	60	2/5/2017 1:46	58	3/5/2017 2:51	59	4/5/2017 3:56	55	5/5/2017 5:01	57	6/5/2017 6:06	61
1/5/2017 0:46	60	2/5/2017 1:51	58	3/5/2017 2:56	60	4/5/2017 4:01	56	5/5/2017 5:06	58	6/5/2017 6:11	61
1/5/2017 0:51	61	2/5/2017 1:56	58	3/5/2017 3:01	59	4/5/2017 4:06	56	5/5/2017 5:11	58	6/5/2017 6:16	61
1/5/2017 0:56	60	2/5/2017 2:01	58	3/5/2017 3:06	60	4/5/2017 4:11	57	5/5/2017 5:16	58	6/5/2017 6:21	61
1/5/2017 1:01	61	2/5/2017 2:06	58	3/5/2017 3:11	58	4/5/2017 4:16	57	5/5/2017 5:21	59	6/5/2017 6:26	56
1/5/2017 1:06	60	2/5/2017 2:11	57	3/5/2017 3:16	59	4/5/2017 4:21	56	5/5/2017 5:26	59	6/5/2017 6:31	43
1/5/2017 1:11	60	2/5/2017 2:16	58	3/5/2017 3:21	59	4/5/2017 4:26	56	5/5/2017 5:31	60	6/5/2017 6:36	53
1/5/2017 1:16	60	2/5/2017 2:21	57	3/5/2017 3:26	58	4/5/2017 4:31	57	5/5/2017 5:36	60	6/5/2017 6:41	55
1/5/2017 1:21	60	2/5/2017 2:26	58	3/5/2017 3:31	58	4/5/2017 4:36	57	5/5/2017 5:41	59	6/5/2017 6:46	53
1/5/2017 1:26	60	2/5/2017 2:31	58	3/5/2017 3:36	59	4/5/2017 4:41	56	5/5/2017 5:46	59	6/5/2017 6:51	58
1/5/2017 1:31	59	2/5/2017 2:36	57	3/5/2017 3:41	59	4/5/2017 4:46	57	5/5/2017 5:51	61	6/5/2017 6:56	54
1/5/2017 1:36	60	2/5/2017 2:41	57	3/5/2017 3:46	58	4/5/2017 4:51	57	5/5/2017 5:56	61	6/5/2017 23:01	53
1/5/2017 1:41	61	2/5/2017 2:46	57	3/5/2017 3:51	58	4/5/2017 4:56	56	5/5/2017 6:01	60	6/5/2017 23:06	51
1/5/2017 1:46	59	2/5/2017 2:51	59	3/5/2017 3:56	58	4/5/2017 5:01	59	5/5/2017 6:06	52	6/5/2017 23:11	56
1/5/2017 1:51	60	2/5/2017 2:56	57	3/5/2017 4:01	58	4/5/2017 5:06	58	5/5/2017 6:11	42	6/5/2017 23:16	62
1/5/2017 1:56	59	2/5/2017 3:01	57	3/5/2017 4:06	57	4/5/2017 5:11	57	5/5/2017 6:16	50	6/5/2017 23:21	54
1/5/2017 2:01	59	2/5/2017 3:06	57	3/5/2017 4:11	57	4/5/2017 5:16	57	5/5/2017 6:21	52	6/5/2017 23:26	62
1/5/2017 2:06	60	2/5/2017 3:11	56	3/5/2017 4:16	58	4/5/2017 5:21	59	5/5/2017 6:26	54	6/5/2017 23:31	53
1/5/2017 2:11	59	2/5/2017 3:16	57	3/5/2017 4:21	58	4/5/2017 5:26	58	5/5/2017 6:31	56	6/5/2017 23:36	56
1/5/2017 2:16	59	2/5/2017 3:21	57	3/5/2017 4:26	58	4/5/2017 5:31	60	5/5/2017 6:36	58	6/5/2017 23:41	62
1/5/2017 2:21	59	2/5/2017 3:26	58	3/5/2017 4:31	59	4/5/2017 5:36	59	5/5/2017 6:41	60	6/5/2017 23:46	62
1/5/2017 2:26	60	2/5/2017 3:31	57	3/5/2017 4:36	57	4/5/2017 5:41	59	5/5/2017 6:46	59	6/5/2017 23:51	57
1/5/2017 2:31	58	2/5/2017 3:36	58	3/5/2017 4:41	58	4/5/2017 5:46	60	5/5/2017 6:51	59	6/5/2017 23:56	62
1/5/2017 2:36	59	2/5/2017 3:41	56	3/5/2017 4:46	58	4/5/2017 5:51	61	5/5/2017 6:56	59	7/5/2017 0:01	61
1/5/2017 2:41	59	2/5/2017 3:46	55	3/5/2017 4:51	59	4/5/2017 5:56	59	5/5/2017 23:01	58	7/5/2017 0:06	62
1/5/2017 2:46	58	2/5/2017 3:51	57	3/5/2017 4:56	59	4/5/2017 6:01	60	5/5/2017 23:06	58	7/5/2017 0:11	61
1/5/2017 2:51	58	2/5/2017 3:56	56	3/5/2017 5:01	59	4/5/2017 6:06	61	5/5/2017 23:11	55	7/5/2017 0:16	46
1/5/2017 2:56	59	2/5/2017 4:01	56	3/5/2017 5:06	59	4/5/2017 6:11	61	5/5/2017 23:16	57	7/5/2017 0:21	62
1/5/2017 3:01	59	2/5/2017 4:06	57	3/5/2017 5:11	58	4/5/2017 6:16	61	5/5/2017 23:21	57	7/5/2017 0:26	62
1/5/2017 3:06	59	2/5/2017 4:11	57	3/5/2017 5:16	59	4/5/2017 6:21	62	5/5/2017 23:26	57	7/5/2017 0:31	61
1/5/2017 3:11	60	2/5/2017 4:16	57	3/5/2017 5:21	58	4/5/2017 6:26	54	5/5/2017 23:31	55	7/5/2017 0:36	61
1/5/2017 3:16	58	2/5/2017 4:21	57	3/5/2017 5:26	58	4/5/2017 6:31	56	5/5/2017 23:36	53	7/5/2017 0:41	61
1/5/2017 3:21	58	2/5/2017 4:26	57	3/5/2017 5:31	59	4/5/2017 6:36	54	5/5/2017 23:41	62	7/5/2017 0:46	60
1/5/2017 3:26	58	2/5/2017 4:31	57	3/5/2017 5:36	59	4/5/2017 6:41	60	5/5/2017 23:46	53	7/5/2017 0:51	61
1/5/2017 3:31	58	2/5/2017 4:36	57	3/5/2017 5:41	59	4/5/2017 6:46	58	5/5/2017 23:51	39	7/5/2017 0:56	61
1/5/2017 3:36	58	2/5/2017 4:41	57	3/5/2017 5:46	60	4/5/2017 6:51	58	5/5/2017 23:56	55	7/5/2017 1:01	60
1/5/2017 3:41	58	2/5/2017 4:46	57	3/5/2017 5:51	60	4/5/2017 6:56	58	6/5/2017 0:01	55	7/5/2017 1:06	60
1/5/2017 3:46	58	2/5/2017 4:51	56	3/5/2017 5:56	60	4/5/2017 23:01	56	6/5/2017 0:06	52	7/5/2017 1:11	60
1/5/2017 3:51	57	2/5/2017 4:56	58	3/5/2017 6:01	59	4/5/2017 23:06	55	6/5/2017 0:11	57	7/5/2017 1:16	60
1/5/2017 3:56	58	2/5/2017 5:01	57	3/5/2017 6:06	60	4/5/2017 23:11	52	6/5/2017 0:16	62	7/5/2017 1:21	60
1/5/2017 4:01	58	2/5/2017 5:06	58	3/5/2017 6:11	60	4/5/2017 23:16	57	6/5/2017 0:21	43	7/5/2017 1:26	61
1/5/2017 4:06	58	2/5/2017 5:11	59	3/5/2017 6:16	60	4/5/2017 23:21	55	6/5/2017 0:26	62	7/5/2017 1:31	59
1/5/2017 4:11	57	2/5/2017 5:16	58	3/5/2017 6:21	60	4/5/2017 23:26	58	6/5/2017 0:31	61	7/5/2017 1:36	60
1/5/2017 4:16	57	2/5/2017 5:21	58	3/5/2017 6:26	61	4/5/2017 23:31	56	6/5/2017 0:36	54	7/5/2017 1:41	61
1/5/2017 4:21	57	2/5/2017 5:26	58	3/5/2017 6:31	60	4/5/2017 23:36	55	6/5/2017 0:41	62	7/5/2017 1:46	60
1/5/2017 4:26	59	2/5/2017 5:31	58	3/5/2017 6:36	51	4/5/2017 23:41	56	6/5/2017 0:46	62	7/5/2017 1:51	60
1/5/2017 4:31	58	2/5/2017 5:36	59	3/5/2017 6:41	62	4/5/2017 23:46	42	6/5/2017 0:51	61	7/5/2017 1:56	60
1/5/2017 4:36	59	2/5/2017 5:41	60	3/5/2017 6:46	46	4/5/2017 23:51	52	6/5/2017 0:56	62	7/5/2017 2:01	62
1/5/2017 4:41	57	2/5/2017 5:46	60	3/5/2017 6:51	62	4/5/2017 23:56	51	6/5/2017 1:01	61	7/5/2017 2:06	61
1/5/2017 4:46	60	2/5/2017 5:51	60	3/5/2017 6:56	61	5/5/2017 0:01	52	6/5/2017 1:06	61	7/5/2017 2:11	60
1/5/2017 4:51	57	2/5/2017 5:56	60	3/5/2017 23:01	62	5/5/2017 0:06	61	6/5/2017 1:11	62	7/5/2017 2:16	60
1/5/2017 4:56	58	2/5/2017 6:01	61	3/5/2017 23:06	53	5/5/2017 0:11	62	6/5/2017 1:16	61	7/5/2017 2:21	60
1/5/2017 5:01	58	2/5/2017 6:06	61	3/5/2017 23:11	62	5/5/2017 0:16	40	6/5/2017 1:21	61	7/5/2017 2:26	60
1/5/2017 5:06	59	2/5/2017 6:11	60	3/5/2017 23:16	61	5/5/2017 0:21	51	6/5/2017 1:26	61	7/5/2017 2:31	61
1/5/2017 5:11	59	2/5/2017 6:16	62	3/5/2017 23:21	62	5/5/2017 0:26	61	6/5/2017 1:31	61	7/5/2017 2:36	60
1/5/2017 5:16	58	2/5/2017 6:21	61	3/5/2017 23:26	47	5/5/2017 0:31	61	6/5/2017 1:36	61	7/5/2017 2:41	60
1/5/2017 5:21	59	2/5/2017 6:26	51	3/5/2017 23:31	62	5/5/2017 0:36	61	6/5/2017 1:41	61	7/5/2017 2:46	60
1/5/2017 5:26	58	2/5/2017 6:31	54	3/5/2017 23:36	61	5/5/2017 0:41	54	6/5/2017 1:46	61	7/5/2017 2:51	61
1/5/2017 5:31	57	2/5/2017 6:36	55	3/5/2017 23:41	42	5/5/2017 0:46	61	6/5/2017 1:51	61	7/5/2017 2:56	60
1/5/2017 5:36	58	2/5/2017 6:41	57	3/5/2017 23:46	62	5/5/2017 0:51	61	6/5/2017 1:56	61	7/5/2017 3:01	60
1/5/2017 5:41	59	2/5/2017 6:46	60	3/5/2017 23:51	62	5/5/2017 0:56	61	6/5/2017 2:01	60	7/5/2017 3:06	61
1/5/2017 5:46	59	2/5/2017 6:51	58	3/5/2017 23:56	60	5/5/2017 1:01	61	6/5/2017 2:06	60	7/5/2017 3:11	60
1/5/2017 5:51	60	2/5/2017 6:56	57	4/5/2017 0:01	60	5/5/2017 1:06	62	6/5/2017 2:11	61	7/5/2017 3:16	60
1/5/2017 5:56	60	2/5/2017 23:01	52	4/5/2017 0:06	61	5/5/2017 1:11	60	6/5/2017 2:16	61	7/5/2017 3:21	59
1/5/2017 6:01	60	2/5/2017 23:06	48	4/5/2017 0:11	60	5/5/2017 1:16	61	6/5/2017 2:21	59	7/5/2017 3:26	59
1/5/2017 6:06	61	2/5/2017 23:11	50	4/5/2017 0:16	60	5/5/2017 1:21	59	6/5/2017 2:26	61	7/5/2017 3:31	60
1/5/2017 6:11	59	2/5/2017 23:16	36	4/5/2017 0:21	60	5/5/2017 1:26	60	6/5/2017 2:31	60	7/5/2017 3:36	60
1/5/2017 6:16	60	2/5/2017 23:21	49	4/5/2017 0:26	60</						

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)											
7/5/2017 6:16	61	8/5/2017 23:21	61	10/5/2017 0:26	61	11/5/2017 1:31	59	12/5/2017 2:36	59	13/5/2017 3:41	59		
7/5/2017 6:21	61	8/5/2017 23:26	61	10/5/2017 0:31	62	11/5/2017 1:36	60	12/5/2017 2:41	58	13/5/2017 3:46	59		
7/5/2017 6:26	62	8/5/2017 23:31	58	10/5/2017 0:36	61	11/5/2017 1:41	59	12/5/2017 2:46	58	13/5/2017 3:51	59		
7/5/2017 6:31	61	8/5/2017 23:36	58	10/5/2017 0:41	61	11/5/2017 1:46	59	12/5/2017 2:51	58	13/5/2017 3:56	58		
7/5/2017 6:36	56	8/5/2017 23:41	55	10/5/2017 0:46	60	11/5/2017 1:51	59	12/5/2017 2:56	58	13/5/2017 4:01	59		
7/5/2017 6:41	54	8/5/2017 23:46	54	10/5/2017 0:51	62	11/5/2017 1:56	58	12/5/2017 3:01	59	13/5/2017 4:06	58		
7/5/2017 6:46	54	8/5/2017 23:51	52	10/5/2017 0:56	60	11/5/2017 2:01	59	12/5/2017 3:06	58	13/5/2017 4:11	59		
7/5/2017 6:51	61	8/5/2017 23:56	58	10/5/2017 1:01	60	11/5/2017 2:06	59	12/5/2017 3:11	59	13/5/2017 4:16	58		
7/5/2017 6:56	60	9/5/2017 0:01	56	10/5/2017 1:06	60	11/5/2017 2:11	59	12/5/2017 3:16	61	13/5/2017 4:21	58		
7/5/2017 23:01	61	9/5/2017 0:06	54	10/5/2017 1:11	60	11/5/2017 2:16	58	12/5/2017 3:21	57	13/5/2017 4:26	58		
7/5/2017 23:06	45	9/5/2017 0:11	53	10/5/2017 1:16	60	11/5/2017 2:21	58	12/5/2017 3:26	58	13/5/2017 4:31	59		
7/5/2017 23:11	51	9/5/2017 0:16	53	10/5/2017 1:21	60	11/5/2017 2:26	58	12/5/2017 3:31	58	13/5/2017 4:36	59		
7/5/2017 23:16	62	9/5/2017 0:21	47	10/5/2017 1:26	59	11/5/2017 2:31	58	12/5/2017 3:36	58	13/5/2017 4:41	59		
7/5/2017 23:21	62	9/5/2017 0:26	62	10/5/2017 1:31	59	11/5/2017 2:36	59	12/5/2017 3:41	58	13/5/2017 4:46	59		
7/5/2017 23:26	62	9/5/2017 0:31	48	10/5/2017 1:36	60	11/5/2017 2:41	59	12/5/2017 3:46	57	13/5/2017 4:51	58		
7/5/2017 23:31	62	9/5/2017 0:36	62	10/5/2017 1:41	60	11/5/2017 2:46	61	12/5/2017 3:51	57	13/5/2017 4:56	59		
7/5/2017 23:36	61	9/5/2017 0:41	62	10/5/2017 1:46	58	11/5/2017 2:51	58	12/5/2017 3:56	57	13/5/2017 5:01	58		
7/5/2017 23:41	62	9/5/2017 0:46	61	10/5/2017 1:51	59	11/5/2017 2:56	57	12/5/2017 4:01	58	13/5/2017 5:06	58		
7/5/2017 23:46	61	9/5/2017 0:51	61	10/5/2017 1:56	58	11/5/2017 3:01	59	12/5/2017 4:06	58	13/5/2017 5:11	59		
7/5/2017 23:51	61	9/5/2017 0:56	61	10/5/2017 2:01	59	11/5/2017 3:06	57	12/5/2017 4:11	57	13/5/2017 5:16	59		
7/5/2017 23:56	61	9/5/2017 1:01	61	10/5/2017 2:06	59	11/5/2017 3:11	58	12/5/2017 4:16	58	13/5/2017 5:21	59		
8/5/2017 0:01	61	9/5/2017 1:06	61	10/5/2017 2:11	58	11/5/2017 3:16	59	12/5/2017 4:21	57	13/5/2017 5:26	58		
8/5/2017 0:06	62	9/5/2017 1:11	60	10/5/2017 2:16	59	11/5/2017 3:21	59	12/5/2017 4:26	57	13/5/2017 5:31	59		
8/5/2017 0:11	61	9/5/2017 1:16	61	10/5/2017 2:21	59	11/5/2017 3:26	57	12/5/2017 4:31	58	13/5/2017 5:36	59		
8/5/2017 0:16	60	9/5/2017 1:21	62	10/5/2017 2:26	59	11/5/2017 3:31	58	12/5/2017 4:36	58	13/5/2017 5:41	59		
8/5/2017 0:21	60	9/5/2017 1:26	48	10/5/2017 2:31	59	11/5/2017 3:36	58	12/5/2017 4:41	57	13/5/2017 5:46	60		
8/5/2017 0:26	62	9/5/2017 1:31	61	10/5/2017 2:36	57	11/5/2017 3:41	57	12/5/2017 4:46	56	13/5/2017 5:51	59		
8/5/2017 0:31	61	9/5/2017 1:36	61	10/5/2017 2:41	57	11/5/2017 3:46	57	12/5/2017 4:51	58	13/5/2017 5:56	60		
8/5/2017 0:36	60	9/5/2017 1:41	61	10/5/2017 2:46	57	11/5/2017 3:51	57	12/5/2017 4:56	57	13/5/2017 6:01	61		
8/5/2017 0:41	59	9/5/2017 1:46	61	10/5/2017 2:51	59	11/5/2017 3:56	58	12/5/2017 5:01	58	13/5/2017 6:06	60		
8/5/2017 0:46	60	9/5/2017 1:51	61	10/5/2017 2:56	57	11/5/2017 4:01	57	12/5/2017 5:06	58	13/5/2017 6:11	60		
8/5/2017 0:51	59	9/5/2017 1:56	62	10/5/2017 3:01	58	11/5/2017 4:06	56	12/5/2017 5:11	57	13/5/2017 6:16	61		
8/5/2017 0:56	59	9/5/2017 2:01	61	10/5/2017 3:06	58	11/5/2017 4:11	57	12/5/2017 5:16	58	13/5/2017 6:21	61		
8/5/2017 1:01	59	9/5/2017 2:06	48	10/5/2017 3:11	59	11/5/2017 4:16	58	12/5/2017 5:21	59	13/5/2017 6:26	62		
8/5/2017 1:06	59	9/5/2017 2:11	40	10/5/2017 3:16	59	11/5/2017 4:21	57	12/5/2017 5:26	59	13/5/2017 6:31	61		
8/5/2017 1:11	60	9/5/2017 2:16	62	10/5/2017 3:21	57	11/5/2017 4:26	57	12/5/2017 5:31	60	13/5/2017 6:36	62		
8/5/2017 1:16	60	9/5/2017 2:21	61	10/5/2017 3:26	57	11/5/2017 4:31	58	12/5/2017 5:36	60	13/5/2017 6:41	62		
8/5/2017 1:21	59	9/5/2017 2:26	61	10/5/2017 3:31	58	11/5/2017 4:36	58	12/5/2017 5:41	59	13/5/2017 6:46	54		
8/5/2017 1:26	59	9/5/2017 2:31	62	10/5/2017 3:36	58	11/5/2017 4:41	58	12/5/2017 5:46	59	13/5/2017 6:51	62		
8/5/2017 1:31	60	9/5/2017 2:36	61	10/5/2017 3:41	58	11/5/2017 4:46	57	12/5/2017 5:51	60	13/5/2017 6:56	56		
8/5/2017 1:36	58	9/5/2017 2:41	61	10/5/2017 3:46	56	11/5/2017 4:51	58	12/5/2017 5:56	60	13/5/2017 23:01	57		
8/5/2017 1:41	58	9/5/2017 2:46	61	10/5/2017 3:51	58	11/5/2017 4:56	58	12/5/2017 6:01	60	13/5/2017 23:06	58		
8/5/2017 1:46	57	9/5/2017 2:51	61	10/5/2017 3:56	58	11/5/2017 5:01	57	12/5/2017 6:06	61	13/5/2017 23:11	57		
8/5/2017 1:51	58	9/5/2017 2:56	51	10/5/2017 4:01	57	11/5/2017 5:06	58	12/5/2017 6:11	48	13/5/2017 23:16	57		
8/5/2017 1:56	59	9/5/2017 3:01	61	10/5/2017 4:06	58	11/5/2017 5:11	58	12/5/2017 6:16	61	13/5/2017 23:21	56		
8/5/2017 2:01	57	9/5/2017 3:06	61	10/5/2017 4:11	58	11/5/2017 5:16	58	12/5/2017 6:21	62	13/5/2017 23:26	58		
8/5/2017 2:06	58	9/5/2017 3:11	61	10/5/2017 4:16	58	11/5/2017 5:21	59	12/5/2017 6:26	57	13/5/2017 23:31	53		
8/5/2017 2:11	58	9/5/2017 3:16	59	10/5/2017 4:21	58	11/5/2017 5:26	59	12/5/2017 6:31	57	13/5/2017 23:36	56		
8/5/2017 2:16	59	9/5/2017 3:21	59	10/5/2017 4:26	58	11/5/2017 5:31	58	12/5/2017 6:36	57	13/5/2017 23:41	57		
8/5/2017 2:21	59	9/5/2017 3:26	60	10/5/2017 4:31	58	11/5/2017 5:36	59	12/5/2017 6:41	59	13/5/2017 23:46	56		
8/5/2017 2:26	58	9/5/2017 3:31	60	10/5/2017 4:36	57	11/5/2017 5:41	59	12/5/2017 6:46	57	13/5/2017 23:51	55		
8/5/2017 2:31	58	9/5/2017 3:36	59	10/5/2017 4:41	58	11/5/2017 5:46	60	12/5/2017 6:51	59	13/5/2017 23:56	50		
8/5/2017 2:36	57	9/5/2017 3:41	59	10/5/2017 4:46	57	11/5/2017 5:51	60	12/5/2017 6:56	58	14/5/2017 0:01	51		
8/5/2017 2:41	57	9/5/2017 3:46	60	10/5/2017 4:51	59	11/5/2017 5:56	60	12/5/2017 23:01	58	14/5/2017 0:06	54		
8/5/2017 2:46	58	9/5/2017 3:51	60	10/5/2017 4:56	58	11/5/2017 6:01	60	12/5/2017 23:06	56	14/5/2017 0:11	54		
8/5/2017 2:51	58	9/5/2017 3:56	59	10/5/2017 5:01	58	11/5/2017 6:06	60	12/5/2017 23:11	57	14/5/2017 0:16	47		
8/5/2017 2:56	56	9/5/2017 4:01	59	10/5/2017 5:06	58	11/5/2017 6:11	61	12/5/2017 23:16	57	14/5/2017 0:21	54		
8/5/2017 3:01	57	9/5/2017 4:06	58	10/5/2017 5:11	58	11/5/2017 6:16	62	12/5/2017 23:21	56	14/5/2017 0:26	52		
8/5/2017 3:06	58	9/5/2017 4:11	58	10/5/2017 5:16	58	11/5/2017 6:21	62	12/5/2017 23:26	56	14/5/2017 0:31	57		
8/5/2017 3:11	57	9/5/2017 4:16	58	10/5/2017 5:21	59	11/5/2017 6:26	53	12/5/2017 23:31	54	14/5/2017 0:36	56		
8/5/2017 3:16	55	9/5/2017 4:21	59	10/5/2017 5:26	58	11/5/2017 6:31	50	12/5/2017 23:36	54	14/5/2017 0:41	48		
8/5/2017 3:21	56	9/5/2017 4:26	59	10/5/2017 5:31	59	11/5/2017 6:36	57	12/5/2017 23:41	51	14/5/2017 0:46	61		
8/5/2017 3:26	57	9/5/2017 4:31	58	10/5/2017 5:36	59	11/5/2017 6:41	58	12/5/2017 23:46	45	14/5/2017 0:51	62		
8/5/2017 3:31	59	9/5/2017 4:36	58	10/5/2017 5:41	59	11/5/2017 6:46	58	12/5/2017 23:51	55	14/5/2017 0:56	61		
8/5/2017 3:36	58	9/5/2017 4:41	57	10/5/2017 5:46	60	11/5/2017 6:51	58	12/5/2017 23:56	47	14/5/2017 1:01	61		
8/5/2017 3:41	57	9/5/2017 4:46	58	10/5/2017 5:51	61	11/5/2017 6:56	57	13/5/2017 0:01	54	14/5/2017 1:06	42		
8/5/2017 3:46	56	9/5/2017 4:51	59	10/5/2017 5:56	61	11/5/2017 23:01	55	13/5/2017 0:06	56	14/5/2017 1:11	61		
8/5/2017 3:51	57	9/5/2017 4:56	59	10/5/2017 6:01	61	11/5/2017 23:06	53	13/5/2017 0:11	62	14/5/2017 1:16	61		
8/5/2017 3:56	57	9/5/2017 5:01	58	10/5/2017 6:06	61	11/5/2017 23:11	54	13/5/2017 0:16	62	14/5/2017 1:21	61		
8/5/2017 4:01	58	9/5/2017 5:06	59	10/5/2017 6:11	62	11/5/2017 23:16	46	13/5/2017 0:21	42	14/5/2017 1:26	61		
8/5/2017 4:06	57	9/5/2017 5:11	57	10/5/2017 6:16	45	11/5/2017 23:21	44	13/5/2017 0:26	54	14/5/2017 1:31	62		
8/5/2017 4:11	57	9/5/2017 5:16	59	10/5/2017 6:21	46	11/5/2017 23:26	55	13/5/2017 0:31	46	14/5/2017 1:36	61		
8/5/2017 4:16	57	9/5/2017 5:21	59	10/5/2017 6:26	55	11/5/2017 23:31	52						

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)									
14/5/2017 4:46	59	15/5/2017 5:51	60	16/5/2017 6:56	63	18/5/2017 0:01	62	19/5/2017 1:06	60	20/5/2017 2:11	60
14/5/2017 4:51	59	15/5/2017 5:56	60	16/5/2017 23:01	56	18/5/2017 0:06	61	19/5/2017 1:11	60	20/5/2017 2:16	61
14/5/2017 4:56	60	15/5/2017 6:01	61	16/5/2017 23:06	54	18/5/2017 0:11	62	19/5/2017 1:16	60	20/5/2017 2:21	60
14/5/2017 5:01	59	15/5/2017 6:06	61	16/5/2017 23:11	50	18/5/2017 0:16	46	19/5/2017 1:21	60	20/5/2017 2:26	60
14/5/2017 5:06	58	15/5/2017 6:11	47	16/5/2017 23:16	55	18/5/2017 0:21	61	19/5/2017 1:26	60	20/5/2017 2:31	60
14/5/2017 5:11	59	15/5/2017 6:16	61	16/5/2017 23:21	53	18/5/2017 0:26	61	19/5/2017 1:31	60	20/5/2017 2:36	60
14/5/2017 5:16	58	15/5/2017 6:21	55	16/5/2017 23:26	40	18/5/2017 0:31	61	19/5/2017 1:36	61	20/5/2017 2:41	60
14/5/2017 5:21	60	15/5/2017 6:26	56	16/5/2017 23:31	53	18/5/2017 0:36	61	19/5/2017 1:41	60	20/5/2017 2:46	59
14/5/2017 5:26	60	15/5/2017 6:31	57	16/5/2017 23:36	47	18/5/2017 0:41	61	19/5/2017 1:46	59	20/5/2017 2:51	60
14/5/2017 5:31	60	15/5/2017 6:36	57	16/5/2017 23:41	49	18/5/2017 0:46	61	19/5/2017 1:51	59	20/5/2017 2:56	59
14/5/2017 5:36	60	15/5/2017 6:41	58	16/5/2017 23:46	50	18/5/2017 0:51	61	19/5/2017 1:56	60	20/5/2017 3:01	59
14/5/2017 5:41	60	15/5/2017 6:46	60	16/5/2017 23:51	61	18/5/2017 0:56	60	19/5/2017 2:01	59	20/5/2017 3:06	59
14/5/2017 5:46	59	15/5/2017 6:51	61	16/5/2017 23:56	62	18/5/2017 1:01	60	19/5/2017 2:06	59	20/5/2017 3:11	59
14/5/2017 5:51	60	15/5/2017 6:56	59	17/5/2017 0:01	62	18/5/2017 1:06	60	19/5/2017 2:11	59	20/5/2017 3:16	59
14/5/2017 5:56	59	15/5/2017 23:01	58	17/5/2017 0:06	61	18/5/2017 1:11	60	19/5/2017 2:16	58	20/5/2017 3:21	58
14/5/2017 6:01	61	15/5/2017 23:06	56	17/5/2017 0:11	61	18/5/2017 1:16	59	19/5/2017 2:21	59	20/5/2017 3:26	59
14/5/2017 6:06	60	15/5/2017 23:11	58	17/5/2017 0:16	61	18/5/2017 1:21	60	19/5/2017 2:26	59	20/5/2017 3:31	58
14/5/2017 6:11	61	15/5/2017 23:16	54	17/5/2017 0:21	50	18/5/2017 1:26	59	19/5/2017 2:31	59	20/5/2017 3:36	58
14/5/2017 6:16	60	15/5/2017 23:21	54	17/5/2017 0:26	61	18/5/2017 1:31	60	19/5/2017 2:36	59	20/5/2017 3:41	58
14/5/2017 6:21	60	15/5/2017 23:26	54	17/5/2017 0:31	52	18/5/2017 1:36	59	19/5/2017 2:41	58	20/5/2017 3:46	61
14/5/2017 6:26	61	15/5/2017 23:31	57	17/5/2017 0:36	60	18/5/2017 1:41	59	19/5/2017 2:46	57	20/5/2017 3:51	58
14/5/2017 6:31	62	15/5/2017 23:36	56	17/5/2017 0:41	61	18/5/2017 1:46	59	19/5/2017 2:51	58	20/5/2017 3:56	58
14/5/2017 6:36	61	15/5/2017 23:41	53	17/5/2017 0:46	61	18/5/2017 1:51	59	19/5/2017 2:56	58	20/5/2017 4:01	59
14/5/2017 6:41	61	15/5/2017 23:46	62	17/5/2017 0:51	61	18/5/2017 1:56	58	19/5/2017 3:01	57	20/5/2017 4:06	58
14/5/2017 6:46	52	15/5/2017 23:51	52	17/5/2017 0:56	60	18/5/2017 2:01	58	19/5/2017 3:06	58	20/5/2017 4:11	59
14/5/2017 6:51	49	15/5/2017 23:56	61	17/5/2017 1:01	61	18/5/2017 2:06	59	19/5/2017 3:11	57	20/5/2017 4:16	59
14/5/2017 6:56	61	16/5/2017 0:01	52	17/5/2017 1:06	61	18/5/2017 2:11	59	19/5/2017 3:16	58	20/5/2017 4:21	59
14/5/2017 23:01	53	16/5/2017 0:06	61	17/5/2017 1:11	60	18/5/2017 2:16	58	19/5/2017 3:21	57	20/5/2017 4:26	59
14/5/2017 23:06	62	16/5/2017 0:11	49	17/5/2017 1:16	60	18/5/2017 2:21	59	19/5/2017 3:26	58	20/5/2017 4:31	58
14/5/2017 23:11	48	16/5/2017 0:16	61	17/5/2017 1:21	59	18/5/2017 2:26	59	19/5/2017 3:31	58	20/5/2017 4:36	58
14/5/2017 23:16	44	16/5/2017 0:21	61	17/5/2017 1:26	60	18/5/2017 2:31	58	19/5/2017 3:36	58	20/5/2017 4:41	59
14/5/2017 23:21	53	16/5/2017 0:26	61	17/5/2017 1:31	60	18/5/2017 2:36	58	19/5/2017 3:41	58	20/5/2017 4:46	58
14/5/2017 23:26	61	16/5/2017 0:31	62	17/5/2017 1:36	61	18/5/2017 2:41	58	19/5/2017 3:46	57	20/5/2017 4:51	59
14/5/2017 23:31	61	16/5/2017 0:36	60	17/5/2017 1:41	59	18/5/2017 2:46	58	19/5/2017 3:51	56	20/5/2017 4:56	58
14/5/2017 23:36	61	16/5/2017 0:41	60	17/5/2017 1:46	60	18/5/2017 2:51	59	19/5/2017 3:56	56	20/5/2017 5:01	59
14/5/2017 23:41	61	16/5/2017 0:46	60	17/5/2017 1:51	60	18/5/2017 2:56	57	19/5/2017 4:01	58	20/5/2017 5:06	59
14/5/2017 23:46	61	16/5/2017 0:51	61	17/5/2017 1:56	59	18/5/2017 3:01	57	19/5/2017 4:06	57	20/5/2017 5:11	58
14/5/2017 23:51	61	16/5/2017 0:56	57	17/5/2017 2:01	60	18/5/2017 3:06	58	19/5/2017 4:11	57	20/5/2017 5:16	59
14/5/2017 23:56	62	16/5/2017 1:01	62	17/5/2017 2:06	59	18/5/2017 3:11	58	19/5/2017 4:16	57	20/5/2017 5:21	59
15/5/2017 0:01	61	16/5/2017 1:06	55	17/5/2017 2:11	59	18/5/2017 3:16	57	19/5/2017 4:21	58	20/5/2017 5:26	59
15/5/2017 0:06	60	16/5/2017 1:11	57	17/5/2017 2:16	59	18/5/2017 3:21	57	19/5/2017 4:26	58	20/5/2017 5:31	59
15/5/2017 0:11	61	16/5/2017 1:16	62	17/5/2017 2:21	58	18/5/2017 3:26	57	19/5/2017 4:31	57	20/5/2017 5:36	60
15/5/2017 0:16	60	16/5/2017 1:21	49	17/5/2017 2:26	59	18/5/2017 3:31	58	19/5/2017 4:36	58	20/5/2017 5:41	59
15/5/2017 0:21	61	16/5/2017 1:26	61	17/5/2017 2:31	58	18/5/2017 3:36	58	19/5/2017 4:41	57	20/5/2017 5:46	60
15/5/2017 0:26	60	16/5/2017 1:31	53	17/5/2017 2:36	58	18/5/2017 3:41	58	19/5/2017 4:46	57	20/5/2017 5:51	61
15/5/2017 0:31	59	16/5/2017 1:36	57	17/5/2017 2:41	57	18/5/2017 3:46	57	19/5/2017 4:51	58	20/5/2017 5:56	60
15/5/2017 0:36	60	16/5/2017 1:41	49	17/5/2017 2:46	58	18/5/2017 3:51	58	19/5/2017 4:56	58	20/5/2017 6:01	60
15/5/2017 0:41	60	16/5/2017 1:46	61	17/5/2017 2:51	58	18/5/2017 3:56	58	19/5/2017 5:01	58	20/5/2017 6:06	60
15/5/2017 0:46	58	16/5/2017 1:51	60	17/5/2017 2:56	59	18/5/2017 4:01	57	19/5/2017 5:06	59	20/5/2017 6:11	61
15/5/2017 0:51	59	16/5/2017 1:56	60	17/5/2017 3:01	59	18/5/2017 4:06	58	19/5/2017 5:11	57	20/5/2017 6:16	61
15/5/2017 0:56	59	16/5/2017 2:01	60	17/5/2017 3:06	59	18/5/2017 4:11	57	19/5/2017 5:16	57	20/5/2017 6:21	61
15/5/2017 1:01	60	16/5/2017 2:06	60	17/5/2017 3:11	57	18/5/2017 4:16	57	19/5/2017 5:21	59	20/5/2017 6:26	61
15/5/2017 1:06	59	16/5/2017 2:11	60	17/5/2017 3:16	57	18/5/2017 4:21	57	19/5/2017 5:26	59	20/5/2017 6:31	62
15/5/2017 1:11	58	16/5/2017 2:16	59	17/5/2017 3:21	58	18/5/2017 4:26	58	19/5/2017 5:31	60	20/5/2017 6:36	61
15/5/2017 1:16	60	16/5/2017 2:21	59	17/5/2017 3:26	56	18/5/2017 4:31	58	19/5/2017 5:36	59	20/5/2017 6:41	54
15/5/2017 1:21	59	16/5/2017 2:26	60	17/5/2017 3:31	58	18/5/2017 4:36	57	19/5/2017 5:41	58	20/5/2017 6:46	52
15/5/2017 1:26	61	16/5/2017 2:31	58	17/5/2017 3:36	58	18/5/2017 4:41	58	19/5/2017 5:46	59	20/5/2017 6:51	55
15/5/2017 1:31	59	16/5/2017 2:36	59	17/5/2017 3:41	58	18/5/2017 4:46	58	19/5/2017 5:51	59	20/5/2017 6:56	52
15/5/2017 1:36	58	16/5/2017 2:41	58	17/5/2017 3:46	58	18/5/2017 4:51	58	19/5/2017 5:56	60	20/5/2017 7:01	55
15/5/2017 1:41	57	16/5/2017 2:46	59	17/5/2017 3:51	57	18/5/2017 4:56	58	19/5/2017 6:01	60	20/5/2017 7:06	49
15/5/2017 1:46	58	16/5/2017 2:51	58	17/5/2017 3:56	58	18/5/2017 5:01	57	19/5/2017 6:06	60	20/5/2017 7:11	56
15/5/2017 1:51	57	16/5/2017 2:56	57	17/5/2017 4:01	56	18/5/2017 5:06	59	19/5/2017 6:11	61	20/5/2017 7:16	48
15/5/2017 1:56	59	16/5/2017 3:01	59	17/5/2017 4:06	57	18/5/2017 5:11	57	19/5/2017 6:16	45	20/5/2017 7:21	52
15/5/2017 2:01	58	16/5/2017 3:06	59	17/5/2017 4:11	56	18/5/2017 5:16	57	19/5/2017 6:21	61	20/5/2017 7:26	62
15/5/2017 2:06	58	16/5/2017 3:11	57	17/5/2017 4:16	59	18/5/2017 5:21	58	19/5/2017 6:26	50	20/5/2017 7:31	50
15/5/2017 2:11	57	16/5/2017 3:16	58	17/5/2017 4:21	58	18/5/2017 5:26	58	19/5/2017 6:31	53	20/5/2017 7:36	43
15/5/2017 2:16	57	16/5/2017 3:21	59	17/5/2017 4:26	58	18/5/2017 5:31	59	19/5/2017 6:36	55	20/5/2017 7:41	62
15/5/2017 2:21	57	16/5/2017 3:26	58	17/5/2017 4:31	59	18/5/2017 5:36	60	19/5/2017 6:41	59	20/5/2017 7:46	62
15/5/2017 2:26	57	16/5/2017 3:31	57	17/5/2017 4:36	57	18/5/2017 5:41	59	19/5/2017 6:46	58	20/5/2017 7:51	61
15/5/2017 2:31	58	16/5/2017 3:36	58	17/5/2017 4:41	58	18/5/2017 5:46	60	19/5/2017 6:51	58	20/5/2017 7:56	62
15/5/2017 2:36	57	16/5/2017 3:41	58	17/5/2017 4:46	58	18/5/2017 5:51	60	19/5/2017 6:56	56	21/5/2017 0:01	62
15/5/2017 2:41	57	16/5/2017 3:46	57	17/5/2017 4:51	59	18/5/2017 5:56	60	19/5/2017 7:01	59	21/5/2017 0:06	61
15/5/2017 2:46	56	16/5/2017 3:51	58	17/5/2017 4:56	58	18/5/2017 6:01	60	19/5/2017 7:06	58	21/5/2017 0:11	62
15/5/2017 2:51	55	16/5/2017 3:56	59	17/5/2017 5:01	58	18/5/2017 6:06	61	19/5/2017 7:11	59	21/5/2017 0:16	43
15/5/2017 2:56	57	16/5/2017 4:01	58	17/5/2017 5:06	59	18/5/2017 6:11	62	19/5/2017 7:16	58	21/5/2017 0:21	61
15/5/2017 3:01	58	16/5/2017 4:06	57	17/5/2017 5:11	58	18/5/2017 6:16	50	19/5/			

Real-time Noise Data		RTN1 (Food and Environmental Hygiene Department Depot)	
21/5/2017 3:16	59	22/5/2017 4:21	58
21/5/2017 3:21	59	22/5/2017 4:26	57
21/5/2017 3:26	59	22/5/2017 4:31	58
21/5/2017 3:31	60	22/5/2017 4:36	58
21/5/2017 3:36	60	22/5/2017 4:41	58
21/5/2017 3:41	59	22/5/2017 4:46	58
21/5/2017 3:46	59	22/5/2017 4:51	58
21/5/2017 3:51	59	22/5/2017 4:56	58
21/5/2017 3:56	59	22/5/2017 5:01	58
21/5/2017 4:01	59	22/5/2017 5:06	59
21/5/2017 4:06	59	22/5/2017 5:11	58
21/5/2017 4:11	59	22/5/2017 5:16	58
21/5/2017 4:16	59	22/5/2017 5:21	59
21/5/2017 4:21	60	22/5/2017 5:26	59
21/5/2017 4:26	59	22/5/2017 5:31	59
21/5/2017 4:31	60	22/5/2017 5:36	61
21/5/2017 4:36	59	22/5/2017 5:41	60
21/5/2017 4:41	59	22/5/2017 5:46	60
21/5/2017 4:46	59	22/5/2017 5:51	61
21/5/2017 4:51	59	22/5/2017 5:56	61
21/5/2017 4:56	58	22/5/2017 6:01	61
21/5/2017 5:01	59	22/5/2017 6:06	61
21/5/2017 5:06	60	22/5/2017 6:11	49
21/5/2017 5:11	58	22/5/2017 6:16	56
21/5/2017 5:16	59	22/5/2017 6:21	57
21/5/2017 5:21	59	22/5/2017 6:26	57
21/5/2017 5:26	60	22/5/2017 6:31	60
21/5/2017 5:31	60	22/5/2017 6:36	58
21/5/2017 5:36	59	22/5/2017 6:41	60
21/5/2017 5:41	60	22/5/2017 6:46	60
21/5/2017 5:46	60	22/5/2017 6:51	57
21/5/2017 5:51	61	22/5/2017 6:56	57
21/5/2017 5:56	60	22/5/2017 7:01	61
21/5/2017 6:01	61	22/5/2017 7:06	61
21/5/2017 6:06	61	22/5/2017 7:11	61
21/5/2017 6:11	60	22/5/2017 7:16	61
21/5/2017 6:16	61	22/5/2017 7:21	59
21/5/2017 6:21	62	22/5/2017 7:26	57
21/5/2017 6:26	49	22/5/2017 7:31	58
21/5/2017 6:31	62	22/5/2017 7:36	57
21/5/2017 6:36	52	22/5/2017 7:41	56
21/5/2017 6:41	48	22/5/2017 7:46	54
21/5/2017 6:46	53	22/5/2017 7:51	45
21/5/2017 6:51	50	22/5/2017 7:56	54
21/5/2017 6:56	50	23/5/2017 0:01	55
21/5/2017 7:01	55	23/5/2017 0:06	52
21/5/2017 7:06	40	23/5/2017 0:11	44
21/5/2017 7:11	54	23/5/2017 0:16	54
21/5/2017 7:16	56	23/5/2017 0:21	49
21/5/2017 7:21	47	23/5/2017 0:26	54
21/5/2017 7:26	54	23/5/2017 0:31	54
21/5/2017 7:31	47	23/5/2017 0:36	45
21/5/2017 7:36	62	23/5/2017 0:41	62
21/5/2017 7:41	62	23/5/2017 0:46	61
21/5/2017 7:46	46	23/5/2017 0:51	61
21/5/2017 7:51	61	23/5/2017 0:56	61
21/5/2017 7:56	54	23/5/2017 1:01	61
22/5/2017 0:01	61	23/5/2017 1:06	61
22/5/2017 0:06	61	23/5/2017 1:11	60
22/5/2017 0:11	62	23/5/2017 1:16	60
22/5/2017 0:16	61	23/5/2017 1:21	60
22/5/2017 0:21	61	23/5/2017 1:26	60
22/5/2017 0:26	61	23/5/2017 1:31	59
22/5/2017 0:31	61	23/5/2017 1:36	60
22/5/2017 0:36	61	23/5/2017 1:41	60
22/5/2017 0:41	62	23/5/2017 1:46	60
22/5/2017 0:46	60	23/5/2017 1:51	59
22/5/2017 0:51	60	23/5/2017 1:56	59
22/5/2017 0:56	60	23/5/2017 2:01	59
22/5/2017 1:01	59	23/5/2017 2:06	60
22/5/2017 1:06	60	23/5/2017 2:11	59
22/5/2017 1:11	58	23/5/2017 2:16	59
22/5/2017 1:16	59	23/5/2017 2:21	60
22/5/2017 1:21	60	23/5/2017 2:26	57
22/5/2017 1:26	59	23/5/2017 2:31	59
22/5/2017 1:31	60	23/5/2017 2:36	59
22/5/2017 1:36	59	23/5/2017 2:41	58
22/5/2017 1:41	59	23/5/2017 2:46	59
22/5/2017 1:46	58	23/5/2017 2:51	59
22/5/2017 1:51	59	23/5/2017 2:56	59
22/5/2017 1:56	58	23/5/2017 3:01	59
22/5/2017 2:01	58	23/5/2017 3:06	59
22/5/2017 2:06	59	23/5/2017 3:11	58
22/5/2017 2:11	57	23/5/2017 3:16	59
22/5/2017 2:16	58	23/5/2017 3:21	57
22/5/2017 2:21	57	23/5/2017 3:26	57
22/5/2017 2:26	57	23/5/2017 3:31	59
22/5/2017 2:31	58	23/5/2017 3:36	58
22/5/2017 2:36	58	23/5/2017 3:41	57
22/5/2017 2:41	58	23/5/2017 3:46	57
22/5/2017 2:46	57	23/5/2017 3:51	57
22/5/2017 2:51	59	23/5/2017 3:56	58
22/5/2017 2:56	58	23/5/2017 4:01	57
22/5/2017 3:01	57	23/5/2017 4:06	57
22/5/2017 3:06	57	23/5/2017 4:11	58
22/5/2017 3:11	58	23/5/2017 4:16	58
22/5/2017 3:16	57	23/5/2017 4:21	58
22/5/2017 3:21	58	23/5/2017 4:26	58
22/5/2017 3:26	56	23/5/2017 4:31	58
22/5/2017 3:31	57	23/5/2017 4:36	58
22/5/2017 3:36	58	23/5/2017 4:41	57
22/5/2017 3:41	58	23/5/2017 4:46	58
22/5/2017 3:46	57	23/5/2017 4:51	59
22/5/2017 3:51	56	23/5/2017 4:56	58
22/5/2017 3:56	57	23/5/2017 5:01	58
22/5/2017 4:01	57	23/5/2017 5:06	59
22/5/2017 4:06	57	23/5/2017 5:11	58
22/5/2017 4:11	57	23/5/2017 5:16	59
22/5/2017 4:16	57	23/5/2017 5:21	58

25/5/2017 23:36	51
25/5/2017 23:41	52
25/5/2017 23:46	62
25/5/2017 23:51	61
25/5/2017 23:56	63
26/5/2017 0:01	62
26/5/2017 0:06	62
26/5/2017 0:11	62
26/5/2017 0:16	62
26/5/2017 0:21	61
26/5/2017 0:26	61
26/5/2017 0:31	61
26/5/2017 0:36	61
26/5/2017 0:41	62
26/5/2017 0:46	61
26/5/2017 0:51	62
26/5/2017 0:56	61
26/5/2017 1:01	61
26/5/2017 1:06	61
26/5/2017 1:11	61
26/5/2017 1:16	60
26/5/2017 1:21	60
26/5/2017 1:26	61
26/5/2017 1:31	60
26/5/2017 1:36	61
26/5/2017 1:41	61
26/5/2017 1:46	59
26/5/2017 1:51	60
26/5/2017 1:56	60
26/5/2017 2:01	59
26/5/2017 2:06	59
26/5/2017 2:11	58
26/5/2017 2:16	58
26/5/2017 2:21	59
26/5/2017 2:26	58
26/5/2017 2:31	59
26/5/2017 2:36	60
26/5/2017 2:41	58
26/5/2017 2:46	58
26/5/2017 2:51	58
26/5/2017 2:56	59
26/5/2017 3:01	57
26/5/2017 3:06	58
26/5/2017 3:11	58
26/5/2017 3:16	58
26/5/2017 3:21	57
26/5/2017 3:26	57
26/5/2017 3:31	59
26/5/2017 3:36	59
26/5/2017 3:41	57
26/5/2017 3:46	58
26/5/2017 3:51	58
26/5/2017 3:56	58
26/5/2017 4:01	58
26/5/2017 4:06	58
26/5/2017 4:11	58
26/5/2017 4:16	58
26/5/2017 4:21	58
26/5/2017 4:26	58
26/5/2017 4:31	58
26/5/2017 4:36	57
26/5/2017 4:41	59
26/5/2017 4:46	58
26/5/2017 4:51	58
26/5/2017 4:56	58
26/5/2017 5:01	57
26/5/2017 5:06	59
26/5/2017 5:11	58
26/5/2017 5:16	60
26/5/2017 5:21	59
26/5/2017 5:26	59
26/5/2017 5:31	60
26/5/2017 5:36	60
26/5/2017 5:41	60
26/5/2017 5:46	60
26/5/2017 5:51	61
26/5/2017 5:56	60
26/5/2017 6:01	61
26/5/2017 6:06	61
26/5/2017 6:11	61
26/5/2017 6:16	48
26/5/2017 6:21	51
26/5/2017 6:26	57
26/5/2017 6:31	54
26/5/2017 6:36	59
26/5/2017 6:41	59
26/5/2017 6:46	60
26/5/2017 6:51	57
26/5/2017 6:56	58
26/5/2017 23:01	58
26/5/2017 23:06	56
26/5/2017 23:11	56
26/5/2017 23:16	54
26/5/2017 23:21	56
26/5/2017 23:26	58
26/5/2017 23:31	54
26/5/2017 23:36	52
26/5/2017 23:41	53
26/5/2017 23:46	50
26/5/2017 23:51	60
26/5/2017 23:56	50

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)													
Normal Day 07:00-19:00															
27/4/2017 7:01	59	4/5/2017 13:01	61	10/5/2017 7:31	69	15/5/2017 14:01	65	20/5/2017 8:31	66	25/5/2017 15:01	65				
27/4/2017 7:31	67	4/5/2017 13:31	65	10/5/2017 8:01	68	15/5/2017 14:31	65	20/5/2017 9:01	66	25/5/2017 15:31	66				
27/4/2017 8:01	66	4/5/2017 14:01	58	10/5/2017 8:31	65	15/5/2017 15:01	63	20/5/2017 9:31	66	25/5/2017 16:01	64				
27/4/2017 8:31	66	4/5/2017 14:31	64	10/5/2017 9:01	66	15/5/2017 15:31	67	20/5/2017 10:01	66	25/5/2017 16:31	62				
27/4/2017 8:31	56	4/5/2017 15:01	62	10/5/2017 9:31	67	15/5/2017 16:01	65	20/5/2017 10:31	65	25/5/2017 17:01	63				
27/4/2017 9:01	59	4/5/2017 15:31	60	10/5/2017 10:01	69	15/5/2017 16:31	63	20/5/2017 11:01	66	25/5/2017 17:31	60				
27/4/2017 9:31	63	4/5/2017 16:01	69	10/5/2017 10:31	69	15/5/2017 17:01	63	20/5/2017 11:31	62	25/5/2017 18:01	59				
27/4/2017 10:01	68	4/5/2017 16:31	59	10/5/2017 11:01	68	15/5/2017 17:31	61	20/5/2017 12:01	61	25/5/2017 18:31	60				
27/4/2017 10:31	62	4/5/2017 17:01	60	10/5/2017 11:31	67	15/5/2017 18:01	59	20/5/2017 12:31	62	26/5/2017 7:01	57				
27/4/2017 11:01	61	4/5/2017 17:31	65	10/5/2017 12:01	62	15/5/2017 18:31	58	20/5/2017 13:01	64	26/5/2017 7:31	60				
27/4/2017 11:31	66	4/5/2017 18:01	64	10/5/2017 12:31	64	16/5/2017 7:01	59	20/5/2017 13:31	65	26/5/2017 8:01	62				
27/4/2017 12:01	65	4/5/2017 18:31	58	10/5/2017 13:01	68	16/5/2017 7:31	55	20/5/2017 14:01	65	26/5/2017 8:31	66				
27/4/2017 12:31	65	5/5/2017 7:01	60	10/5/2017 13:31	68	16/5/2017 8:01	66	20/5/2017 14:31	66	26/5/2017 9:01	66				
27/4/2017 13:01	56	5/5/2017 7:31	60	10/5/2017 14:01	68	16/5/2017 8:31	55	20/5/2017 15:01	65	26/5/2017 9:31	65				
27/4/2017 13:31	64	5/5/2017 8:01	66	10/5/2017 14:31	66	16/5/2017 9:01	66	20/5/2017 15:31	65	26/5/2017 10:01	66				
27/4/2017 14:01	62	5/5/2017 8:31	65	10/5/2017 15:01	66	16/5/2017 9:31	67	20/5/2017 16:01	65	26/5/2017 10:31	66				
27/4/2017 14:31	64	5/5/2017 9:01	68	10/5/2017 15:31	61	16/5/2017 10:01	67	20/5/2017 16:31	64	26/5/2017 11:01	67				
27/4/2017 15:01	66	5/5/2017 9:31	68	10/5/2017 16:01	55	16/5/2017 10:31	65	20/5/2017 17:01	64	26/5/2017 11:31	64				
27/4/2017 15:31	66	5/5/2017 10:01	69	10/5/2017 16:31	67	16/5/2017 11:01	65	20/5/2017 17:31	61	26/5/2017 12:01	61				
27/4/2017 16:01	67	5/5/2017 10:31	67	10/5/2017 17:01	66	16/5/2017 11:31	62	20/5/2017 18:01	60	26/5/2017 12:31	61				
27/4/2017 16:31	61	5/5/2017 11:01	65	10/5/2017 17:31	60	16/5/2017 12:01	59	20/5/2017 18:31	58	26/5/2017 13:01	64				
27/4/2017 17:01	57	5/5/2017 11:31	65	10/5/2017 18:01	59	16/5/2017 12:31	59	22/5/2017 7:01	58	26/5/2017 13:31	67				
27/4/2017 17:31	66	5/5/2017 12:01	66	10/5/2017 18:31	59	16/5/2017 13:01	65	22/5/2017 7:31	62	26/5/2017 14:01	66				
27/4/2017 18:01	62	5/5/2017 12:31	65	11/5/2017 7:01	58	16/5/2017 13:31	66	22/5/2017 8:01	65	26/5/2017 14:31	65				
27/4/2017 18:31	60	5/5/2017 13:01	67	11/5/2017 7:31	61	16/5/2017 14:01	65	22/5/2017 8:31	67	26/5/2017 15:01	64				
28/4/2017 7:01	61	5/5/2017 13:31	65	11/5/2017 8:01	65	16/5/2017 14:31	65	22/5/2017 9:01	60	26/5/2017 15:31	65				
28/4/2017 7:31	65	5/5/2017 14:01	64	11/5/2017 8:31	64	16/5/2017 15:01	67	22/5/2017 9:31	66	26/5/2017 16:01	65				
28/4/2017 8:01	66	5/5/2017 14:31	58	11/5/2017 9:01	66	16/5/2017 15:31	65	22/5/2017 10:01	66	26/5/2017 16:31	64				
28/4/2017 8:31	67	5/5/2017 15:01	66	11/5/2017 9:31	59	16/5/2017 16:01	61	22/5/2017 10:31	70	26/5/2017 17:01	63				
28/4/2017 9:01	67	5/5/2017 15:31	60	11/5/2017 10:01	63	16/5/2017 16:31	60	22/5/2017 11:01	63	26/5/2017 17:31	61				
28/4/2017 9:31	60	5/5/2017 16:01	63	11/5/2017 10:31	64	16/5/2017 17:01	62	22/5/2017 11:31	66	26/5/2017 18:01	63				
28/4/2017 10:01	59	5/5/2017 16:31	66	11/5/2017 11:01	63	16/5/2017 17:31	61	22/5/2017 12:01	59	26/5/2017 18:31	61				
28/4/2017 10:31	59	5/5/2017 17:01	65	11/5/2017 11:31	65	16/5/2017 18:01	60	22/5/2017 12:31	64						
28/4/2017 11:01	61	5/5/2017 17:31	64	11/5/2017 12:01	61	16/5/2017 18:31	59	22/5/2017 13:01	65	Normal Day 19:00-23:00					
28/4/2017 11:31	65	5/5/2017 18:01	63	11/5/2017 12:31	65	17/5/2017 7:01	57	22/5/2017 13:31	59	Sunday & Holiday					
28/4/2017 12:01	63	5/5/2017 18:31	59	11/5/2017 13:01	67	17/5/2017 7:31	59	22/5/2017 14:01	64	07:00-23:00					
28/4/2017 12:31	61	6/5/2017 7:01	59	11/5/2017 13:31	63	17/5/2017 8:01	63	22/5/2017 14:31	67						
28/4/2017 13:01	66	6/5/2017 7:31	62	11/5/2017 14:01	59	17/5/2017 8:31	63	22/5/2017 15:01	67	27/4/2017 19:01	58				
28/4/2017 13:31	59	6/5/2017 8:01	64	11/5/2017 14:31	67	17/5/2017 9:01	64	22/5/2017 15:31	67	27/4/2017 19:06	57				
28/4/2017 14:01	62	6/5/2017 8:31	66	11/5/2017 15:01	66	17/5/2017 9:31	61	22/5/2017 16:01	66	27/4/2017 19:11	58				
28/4/2017 14:31	67	6/5/2017 9:01	63	11/5/2017 15:31	58	17/5/2017 10:01	61	22/5/2017 16:31	66	27/4/2017 19:16	58				
28/4/2017 15:01	47	6/5/2017 9:31	64	11/5/2017 16:01	63	17/5/2017 10:31	64	22/5/2017 17:01	65	27/4/2017 19:21	58				
28/4/2017 15:31	67	6/5/2017 10:01	56	11/5/2017 16:31	67	17/5/2017 11:01	67	22/5/2017 17:31	61	27/4/2017 19:26	58				
28/4/2017 16:01	66	6/5/2017 10:31	52	11/5/2017 17:01	67	17/5/2017 11:31	62	22/5/2017 18:01	60	27/4/2017 19:31	59				
28/4/2017 16:31	65	6/5/2017 11:01	67	11/5/2017 17:31	64	17/5/2017 12:01	59	22/5/2017 18:31	59	27/4/2017 19:36	59				
28/4/2017 17:01	65	6/5/2017 11:31	63	11/5/2017 18:01	63	17/5/2017 12:31	60	23/5/2017 7:01	59	27/4/2017 19:41	61				
28/4/2017 17:31	63	6/5/2017 12:01	61	11/5/2017 18:31	61	17/5/2017 13:01	65	23/5/2017 7:31	65	27/4/2017 19:46	58				
28/4/2017 18:01	61	6/5/2017 12:31	64	12/5/2017 7:01	58	17/5/2017 13:31	57	23/5/2017 8:01	66	27/4/2017 19:51	61				
28/4/2017 18:31	61	6/5/2017 13:01	66	12/5/2017 7:31	62	17/5/2017 14:01	67	23/5/2017 8:31	59	27/4/2017 19:56	58				
29/4/2017 7:01	60	6/5/2017 13:31	67	12/5/2017 8:01	66	17/5/2017 14:31	67	23/5/2017 9:01	66	27/4/2017 20:01	58				
29/4/2017 7:31	63	6/5/2017 14:01	67	12/5/2017 8:31	64	17/5/2017 15:01	66	23/5/2017 9:31	62	27/4/2017 20:06	58				
29/4/2017 8:01	65	6/5/2017 14:31	67	12/5/2017 9:01	65	17/5/2017 15:31	66	23/5/2017 10:01	65	27/4/2017 20:11	58				
29/4/2017 8:31	57	6/5/2017 15:01	65	12/5/2017 9:31	66	17/5/2017 16:01	67	23/5/2017 10:31	59	27/4/2017 20:16	59				
29/4/2017 9:01	67	6/5/2017 15:31	66	12/5/2017 10:01	66	17/5/2017 16:31	66	23/5/2017 11:01	67	27/4/2017 20:21	59				
29/4/2017 9:31	63	6/5/2017 16:01	65	12/5/2017 10:31	67	17/5/2017 17:01	65	23/5/2017 11:31	64	27/4/2017 20:26	58				
29/4/2017 10:01	62	6/5/2017 16:31	64	12/5/2017 11:01	64	17/5/2017 17:31	60	23/5/2017 12:01	63	27/4/2017 20:31	58				
29/4/2017 10:31	63	6/5/2017 17:01	65	12/5/2017 11:31	67	17/5/2017 18:01	60	23/5/2017 12:31	62	27/4/2017 20:36	58				
29/4/2017 11:01	65	6/5/2017 17:31	63	12/5/2017 12:01	65	17/5/2017 18:31	60	23/5/2017 13:01	66	27/4/2017 20:41	57				
29/4/2017 11:31	63	6/5/2017 18:01	63	12/5/2017 12:31	60	18/5/2017 7:01	57	23/5/2017 13:31	62	27/4/2017 20:46	58				
29/4/2017 12:01	63	6/5/2017 18:31	59	12/5/2017 13:01	66	18/5/2017 7:31	59	23/5/2017 14:01	64	27/4/2017 20:51	58				
29/4/2017 12:31	61	8/5/2017 7:01	60	12/5/2017 13:31	69	18/5/2017 8:01	65	23/5/2017 14:31	64	27/4/2017 20:56	58				
29/4/2017 13:01	60	8/5/2017 7:31	62	12/5/2017 14:01	67	18/5/2017 8:31	67	23/5/2017 15:01	61	27/4/2017 21:01	58				
29/4/2017 13:31	61	8/5/2017 8:01	64	12/5/2017 14:31	67	18/5/2017 9:01	67	23/5/2017 15:31	65	27/4/2017 21:06	57				
29/4/2017 14:01	67	8/5/2017 8:31	53	12/5/2017 15:01	64	18/5/2017 9:31	57	23/5/2017 16:01	66	27/4/2017 21:11	56				
29/4/2017 14:31	67	8/5/2017 9:01	67	12/5/2017 15:31	57	18/5/2017 10:01	60	23/5/2017 16:31	64	27/4/2017 21:16	57				
29/4/2017 15:01	66	8/5/2017 9:31	63	12/5/2017 16:01	65	18/5/2017 10:31	56	23/5/2017 17:01	63	27/4/2017 21:21	61				
29/4/2017 15:31	65	8/5/2017 10:01	61	12/5/2017 16:31	65	18/5/2017 11:01	64	23/5/2017 17:31	54	27/4/2017 21:26	57				
29/4/2017 16:01	66	8/5/2017 10:31	67	12/5/2017 17:01	65	18/5/2017 11:31	64	23/5/2017 18:01	68	27/4/2017 21:31	57				
29/4/2017 16:31	67	8/5/2017 11:01	60	12/5/2017 17:31	63	18/5/2017 12:01	60	23/5/2017 18:31	65	27/4/2017 21:36	57				
29/4/2017 17:01	65	8/5/2017 11:31	57	12/5/2017 18:01	63	18/5/2017 12:31	60	24/5/2017 7:01	67	27/4/2017 21:41	59				
29/4/2017 17:31	63	8/5/2017 12:01	64	12/5/2017 18:31	61	18/5/2017 13:01	67	24/5/2017 7:31	67	27/4/2017 21:46	56				
29/4/2017 18:01	61	8/5/2017 12:31	64	13/5/2017 7:01	61	18/5/2017 13:31	29	24/5/2017 8:01	64	27/4/2017 21:51	57				
29/4/2017 18:31	59	8/5/2017 13:01	65	13/5/2017 7:31	64	18/5/2017 14:01	67	24/5/2017 8:31	65	27/4/2017 21:56	60				
2/5/2017 7:01	60	8/5/2017 13:31	52	13/5/2017 8:01	63	18/5/2017 14:31	67	24/5/2017 9:01	66	27/4/2017 22:01	57				
2/5/2017 7:31	64	8/5/2017 14:01	66	13/5/2017 8:31	66	18/5/2017 15:01	66	24/5/2017 9:31	67	27/4/2017 22:06	57				
2/5/2017 8:01	66														

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)							
28/4/2017 21:01	57	30/4/2017 10:06	58	30/4/2017 19:11	58	1/5/2017 12:16	57	1/5/2017 21:21	57
28/4/2017 21:06	58	30/4/2017 10:11	61	30/4/2017 19:16	58	1/5/2017 12:21	57	1/5/2017 21:26	56
28/4/2017 21:11	57	30/4/2017 10:16	58	30/4/2017 19:21	57	1/5/2017 12:26	57	1/5/2017 21:31	56
28/4/2017 21:16	59	30/4/2017 10:21	58	30/4/2017 19:26	57	1/5/2017 12:31	57	1/5/2017 21:36	58
28/4/2017 21:21	60	30/4/2017 10:26	60	30/4/2017 19:31	58	1/5/2017 12:36	57	1/5/2017 21:41	57
28/4/2017 21:26	57	30/4/2017 10:31	58	30/4/2017 19:36	59	1/5/2017 12:41	57	1/5/2017 21:46	57
28/4/2017 21:31	57	30/4/2017 10:36	58	30/4/2017 19:41	58	1/5/2017 12:46	58	1/5/2017 21:51	58
28/4/2017 21:36	58	30/4/2017 10:41	59	30/4/2017 19:46	58	1/5/2017 12:51	57	1/5/2017 21:56	58
28/4/2017 21:41	57	30/4/2017 10:46	59	30/4/2017 19:51	58	1/5/2017 12:56	57	1/5/2017 22:01	58
28/4/2017 21:46	59	30/4/2017 10:51	59	30/4/2017 19:56	58	1/5/2017 13:01	57	1/5/2017 22:06	58
28/4/2017 21:51	57	30/4/2017 10:56	61	30/4/2017 20:01	56	1/5/2017 13:06	58	1/5/2017 22:11	56
28/4/2017 21:56	57	30/4/2017 11:01	59	30/4/2017 20:06	58	1/5/2017 13:11	57	1/5/2017 22:16	58
28/4/2017 22:01	58	30/4/2017 11:06	58	30/4/2017 20:11	58	1/5/2017 13:16	57	1/5/2017 22:21	57
28/4/2017 22:06	58	30/4/2017 11:11	58	30/4/2017 20:16	57	1/5/2017 13:21	57	1/5/2017 22:26	56
28/4/2017 22:11	59	30/4/2017 11:16	58	30/4/2017 20:21	59	1/5/2017 13:26	57	1/5/2017 22:31	57
28/4/2017 22:16	58	30/4/2017 11:21	60	30/4/2017 20:26	57	1/5/2017 13:31	56	1/5/2017 22:36	56
28/4/2017 22:21	57	30/4/2017 11:26	58	30/4/2017 20:31	57	1/5/2017 13:36	59	1/5/2017 22:41	56
28/4/2017 22:26	58	30/4/2017 11:31	59	30/4/2017 20:36	60	1/5/2017 13:41	57	1/5/2017 22:46	56
28/4/2017 22:31	59	30/4/2017 11:36	59	30/4/2017 20:41	58	1/5/2017 13:46	57	1/5/2017 22:51	57
28/4/2017 22:36	61	30/4/2017 11:41	59	30/4/2017 20:46	57	1/5/2017 13:51	57	1/5/2017 22:56	58
28/4/2017 22:41	60	30/4/2017 11:46	58	30/4/2017 20:51	58	1/5/2017 13:56	56	2/5/2017 19:01	60
28/4/2017 22:46	57	30/4/2017 11:51	57	30/4/2017 20:56	57	1/5/2017 14:01	57	2/5/2017 19:06	58
28/4/2017 22:51	58	30/4/2017 11:56	57	30/4/2017 21:01	58	1/5/2017 14:06	57	2/5/2017 19:11	58
28/4/2017 22:56	57	30/4/2017 12:01	57	30/4/2017 21:06	56	1/5/2017 14:11	57	2/5/2017 19:16	57
29/4/2017 19:01	60	30/4/2017 12:06	57	30/4/2017 21:11	56	1/5/2017 14:16	57	2/5/2017 19:21	57
29/4/2017 19:06	59	30/4/2017 12:11	57	30/4/2017 21:16	57	1/5/2017 14:21	57	2/5/2017 19:26	58
29/4/2017 19:11	58	30/4/2017 12:16	57	30/4/2017 21:21	58	1/5/2017 14:26	57	2/5/2017 19:31	58
29/4/2017 19:16	59	30/4/2017 12:21	57	30/4/2017 21:26	57	1/5/2017 14:31	62	2/5/2017 19:36	61
29/4/2017 19:21	60	30/4/2017 12:26	57	30/4/2017 21:31	57	1/5/2017 14:36	59	2/5/2017 19:41	58
29/4/2017 19:26	60	30/4/2017 12:31	57	30/4/2017 21:36	56	1/5/2017 14:41	57	2/5/2017 19:46	59
29/4/2017 19:31	61	30/4/2017 12:36	57	30/4/2017 21:41	57	1/5/2017 14:46	58	2/5/2017 19:51	58
29/4/2017 19:36	59	30/4/2017 12:41	58	30/4/2017 21:46	58	1/5/2017 14:51	56	2/5/2017 19:56	58
29/4/2017 19:41	58	30/4/2017 12:46	57	30/4/2017 21:51	60	1/5/2017 14:56	57	2/5/2017 20:01	59
29/4/2017 19:46	59	30/4/2017 12:51	58	30/4/2017 21:56	56	1/5/2017 15:01	57	2/5/2017 20:06	59
29/4/2017 19:51	57	30/4/2017 12:56	57	30/4/2017 22:01	56	1/5/2017 15:06	58	2/5/2017 20:11	58
29/4/2017 19:56	56	30/4/2017 13:01	57	30/4/2017 22:06	55	1/5/2017 15:11	61	2/5/2017 20:16	59
29/4/2017 20:01	57	30/4/2017 13:06	58	30/4/2017 22:11	56	1/5/2017 15:16	57	2/5/2017 20:21	59
29/4/2017 20:06	60	30/4/2017 13:11	57	30/4/2017 22:16	59	1/5/2017 15:21	56	2/5/2017 20:26	58
29/4/2017 20:11	61	30/4/2017 13:16	58	30/4/2017 22:21	61	1/5/2017 15:26	58	2/5/2017 20:31	57
29/4/2017 20:16	57	30/4/2017 13:21	58	30/4/2017 22:26	59	1/5/2017 15:31	59	2/5/2017 20:36	61
29/4/2017 20:21	58	30/4/2017 13:26	59	30/4/2017 22:31	56	1/5/2017 15:36	57	2/5/2017 20:41	58
29/4/2017 20:26	57	30/4/2017 13:31	57	30/4/2017 22:36	56	1/5/2017 15:41	56	2/5/2017 20:46	58
29/4/2017 20:31	61	30/4/2017 13:36	58	30/4/2017 22:41	58	1/5/2017 15:46	57	2/5/2017 20:51	57
29/4/2017 20:36	59	30/4/2017 13:41	58	30/4/2017 22:46	55	1/5/2017 15:51	58	2/5/2017 20:56	57
29/4/2017 20:41	57	30/4/2017 13:46	58	30/4/2017 22:51	57	1/5/2017 15:56	57	2/5/2017 21:01	58
29/4/2017 20:46	57	30/4/2017 13:51	57	30/4/2017 22:56	58	1/5/2017 16:01	57	2/5/2017 21:06	59
29/4/2017 20:51	56	30/4/2017 13:56	57	1/5/2017 7:01	55	1/5/2017 16:06	58	2/5/2017 21:11	59
29/4/2017 20:56	58	30/4/2017 14:01	59	1/5/2017 7:06	54	1/5/2017 16:11	57	2/5/2017 21:16	57
29/4/2017 21:01	58	30/4/2017 14:06	59	1/5/2017 7:11	55	1/5/2017 16:16	57	2/5/2017 21:21	56
29/4/2017 21:06	59	30/4/2017 14:11	57	1/5/2017 7:16	61	1/5/2017 16:21	57	2/5/2017 21:26	59
29/4/2017 21:11	57	30/4/2017 14:16	58	1/5/2017 7:21	55	1/5/2017 16:26	56	2/5/2017 21:31	57
29/4/2017 21:16	60	30/4/2017 14:21	56	1/5/2017 7:26	56	1/5/2017 16:31	58	2/5/2017 21:36	56
29/4/2017 21:21	58	30/4/2017 14:26	57	1/5/2017 7:31	56	1/5/2017 16:36	56	2/5/2017 21:41	56
29/4/2017 21:26	57	30/4/2017 14:31	58	1/5/2017 7:36	57	1/5/2017 16:41	57	2/5/2017 21:46	60
29/4/2017 21:31	59	30/4/2017 14:36	58	1/5/2017 7:41	56	1/5/2017 16:46	57	2/5/2017 21:51	57
29/4/2017 21:36	57	30/4/2017 14:41	58	1/5/2017 7:46	56	1/5/2017 16:51	57	2/5/2017 21:56	56
29/4/2017 21:41	57	30/4/2017 14:46	58	1/5/2017 7:51	59	1/5/2017 16:56	57	2/5/2017 22:01	57
29/4/2017 21:46	57	30/4/2017 14:51	58	1/5/2017 7:56	56	1/5/2017 17:01	58	2/5/2017 22:06	58
29/4/2017 21:51	59	30/4/2017 14:56	59	1/5/2017 8:01	59	1/5/2017 17:06	57	2/5/2017 22:11	57
29/4/2017 21:56	59	30/4/2017 15:01	59	1/5/2017 8:06	55	1/5/2017 17:11	57	2/5/2017 22:16	57
29/4/2017 22:01	58	30/4/2017 15:06	57	1/5/2017 8:11	56	1/5/2017 17:16	57	2/5/2017 22:21	59
29/4/2017 22:06	57	30/4/2017 15:11	58	1/5/2017 8:16	57	1/5/2017 17:21	57	2/5/2017 22:26	60
29/4/2017 22:11	57	30/4/2017 15:16	58	1/5/2017 8:21	59	1/5/2017 17:26	59	2/5/2017 22:31	62
29/4/2017 22:16	58	30/4/2017 15:21	59	1/5/2017 8:26	58	1/5/2017 17:31	58	2/5/2017 22:36	58
29/4/2017 22:21	57	30/4/2017 15:26	60	1/5/2017 8:31	57	1/5/2017 17:36	59	2/5/2017 22:41	57
29/4/2017 22:26	56	30/4/2017 15:31	58	1/5/2017 8:36	57	1/5/2017 17:41	58	2/5/2017 22:46	58
29/4/2017 22:31	58	30/4/2017 15:36	59	1/5/2017 8:41	58	1/5/2017 17:46	58	2/5/2017 22:51	57
29/4/2017 22:36	59	30/4/2017 15:41	58	1/5/2017 8:46	57	1/5/2017 17:51	57	2/5/2017 22:56	57
29/4/2017 22:41	57	30/4/2017 15:46	58	1/5/2017 8:51	58	1/5/2017 17:56	57	3/5/2017 7:01	57
29/4/2017 22:46	56	30/4/2017 15:51	58	1/5/2017 8:56	58	1/5/2017 18:01	61	3/5/2017 7:06	56
29/4/2017 22:51	56	30/4/2017 15:56	59	1/5/2017 9:01	58	1/5/2017 18:06	57	3/5/2017 7:11	56
29/4/2017 22:56	56	30/4/2017 16:01	60	1/5/2017 9:06	59	1/5/2017 18:11	57	3/5/2017 7:16	56
30/4/2017 7:01	55	30/4/2017 16:06	60	1/5/2017 9:11	57	1/5/2017 18:16	54	3/5/2017 7:21	56
30/4/2017 7:06	55	30/4/2017 16:11	59	1/5/2017 9:16	58	1/5/2017 18:21	58	3/5/2017 7:26	57
30/4/2017 7:11	57	30/4/2017 16:16	53	1/5/2017 9:21	57	1/5/2017 18:26	57	3/5/2017 7:31	56
30/4/2017 7:16	55	30/4/2017 16:21	59	1/5/2017 9:26	58	1/5/2017 18:31	58	3/5/2017 7:36	56
30/4/2017 7:21	57	30/4/2017 16:26	58	1/5/2017 9:31	57	1/5/2017 18:36	58	3/5/2017 7:41	57
30/4/2017 7:26	55	30/4/2017 16:31	58	1/5/2017 9:36	57	1/5/2017 18:41	58	3/5/2017 7:46	57
30/4/2017 7:31	55	30/4/2017 16:36	59	1/5/2017 9:41	57	1/5/2017 18:46	57	3/5/2017 7:51	57
30/4/2017 7:36	57	30/4/2017 16:41	57	1/5/2017 9:46	57	1/5/2017 18:51	58	3/5/2017 7:56	58
30/4/2017 7:41	57	30/4/2017 16:46	61	1/5/2017 9:51	57	1/5/2017 18:56	59	3/5/2017 8:01	58
30/4/2017 7:46	56	30/4/2017 16:51	59	1/5/2017 9:56	57	1/5/2017 19:01	57	3/5/2017 8:06	59
30/4/2017 7:51	57	30/4/2017 16:56	58	1/5/2017 10:01	56	1/5/2017 19:06	56	3/5/2017 8:11	58
30/4/2017 7:56	58	30/4/2017 17:01	58	1/5/2017 10:06	56	1/5/2017 19:11	57	3/5/2017 8:16	60
30/4/2017 8:01	56	30/4/2017 17:06	58	1/5/2017 10:11	57	1/5/2017 19:16	58	3/5/2017 8:21	58
30/4/2017 8:06	56	30/4/2017 17:11	56	1/5/2017 10:16	58	1/5/2017 19:21	58	3/5/2017 8:26	58
30/4/2017 8:11	56	30/4/2017 17:16	60	1/5/2017 10:21	57	1/5/2017 19:26	57	3/5/2017 8:31	57
30/4/2017 8:16	58	30/4/2017 17:21	58	1/5/2017 10:26	57	1/5/2017 19:31	58	3/5/2017 8:36	57
30/4/2017 8:21	57	30/4/2017 17:26	59	1/5/2017 10:31	61	1/5/2017 19:36	58	3/5/2017 8:41	57
30/4/2017 8:26	57	30/4/2017 17:31	59	1/5					

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)											
3/5/2017 19:31	57	5/5/2017 20:36	57	7/5/2017 9:41	57	7/5/2017 18:46	58	9/5/2017 19:51	57	11/5/2017 20:56	58		
3/5/2017 19:36	58	5/5/2017 20:41	59	7/5/2017 9:46	57	7/5/2017 18:51	57	9/5/2017 19:56	57	11/5/2017 21:01	60		
3/5/2017 19:41	60	5/5/2017 20:46	56	7/5/2017 9:51	58	7/5/2017 18:56	58	9/5/2017 20:01	58	11/5/2017 21:06	57		
3/5/2017 19:46	54	5/5/2017 20:51	56	7/5/2017 9:56	57	7/5/2017 19:01	58	9/5/2017 20:06	57	11/5/2017 21:11	57		
3/5/2017 19:51	57	5/5/2017 20:56	56	7/5/2017 10:01	59	7/5/2017 19:06	58	9/5/2017 20:11	58	11/5/2017 21:16	57		
3/5/2017 19:56	58	5/5/2017 21:01	57	7/5/2017 10:06	59	7/5/2017 19:11	56	9/5/2017 20:16	58	11/5/2017 21:21	57		
3/5/2017 20:01	58	5/5/2017 21:06	57	7/5/2017 10:11	57	7/5/2017 19:16	58	9/5/2017 20:21	58	11/5/2017 21:26	57		
3/5/2017 20:06	57	5/5/2017 21:11	61	7/5/2017 10:16	59	7/5/2017 19:21	57	9/5/2017 20:26	57	11/5/2017 21:31	57		
3/5/2017 20:11	57	5/5/2017 21:16	57	7/5/2017 10:21	58	7/5/2017 19:26	57	9/5/2017 20:31	57	11/5/2017 21:36	58		
3/5/2017 20:16	57	5/5/2017 21:21	57	7/5/2017 10:26	57	7/5/2017 19:31	58	9/5/2017 20:36	56	11/5/2017 21:41	56		
3/5/2017 20:21	58	5/5/2017 21:26	58	7/5/2017 10:31	58	7/5/2017 19:36	62	9/5/2017 20:41	55	11/5/2017 21:46	57		
3/5/2017 20:26	58	5/5/2017 21:31	57	7/5/2017 10:36	58	7/5/2017 19:41	57	9/5/2017 20:46	56	11/5/2017 21:51	56		
3/5/2017 20:31	59	5/5/2017 21:36	57	7/5/2017 10:41	58	7/5/2017 19:46	57	9/5/2017 20:51	56	11/5/2017 21:56	56		
3/5/2017 20:36	57	5/5/2017 21:41	57	7/5/2017 10:46	57	7/5/2017 19:51	58	9/5/2017 20:56	56	11/5/2017 22:01	57		
3/5/2017 20:41	58	5/5/2017 21:46	57	7/5/2017 10:51	58	7/5/2017 19:56	58	9/5/2017 21:01	57	11/5/2017 22:06	58		
3/5/2017 20:46	56	5/5/2017 21:51	57	7/5/2017 10:56	57	7/5/2017 20:01	57	9/5/2017 21:06	57	11/5/2017 22:11	59		
3/5/2017 20:51	56	5/5/2017 21:56	57	7/5/2017 11:01	57	7/5/2017 20:06	57	9/5/2017 21:11	57	11/5/2017 22:16	57		
3/5/2017 20:56	57	5/5/2017 22:01	57	7/5/2017 11:06	58	7/5/2017 20:11	58	9/5/2017 21:16	57	11/5/2017 22:21	58		
3/5/2017 21:01	58	5/5/2017 22:06	57	7/5/2017 11:11	59	7/5/2017 20:16	60	9/5/2017 21:21	58	11/5/2017 22:26	57		
3/5/2017 21:06	57	5/5/2017 22:11	57	7/5/2017 11:16	57	7/5/2017 20:21	57	9/5/2017 21:26	58	11/5/2017 22:31	58		
3/5/2017 21:11	56	5/5/2017 22:16	58	7/5/2017 11:21	57	7/5/2017 20:26	57	9/5/2017 21:31	57	11/5/2017 22:36	59		
3/5/2017 21:16	57	5/5/2017 22:21	57	7/5/2017 11:26	58	7/5/2017 20:31	67	9/5/2017 21:36	58	11/5/2017 22:41	58		
3/5/2017 21:21	56	5/5/2017 22:26	58	7/5/2017 11:31	58	7/5/2017 20:36	60	9/5/2017 21:41	57	11/5/2017 22:46	57		
3/5/2017 21:26	56	5/5/2017 22:31	57	7/5/2017 11:36	58	7/5/2017 20:41	56	9/5/2017 21:46	56	11/5/2017 22:51	56		
3/5/2017 21:31	56	5/5/2017 22:36	57	7/5/2017 11:41	58	7/5/2017 20:46	57	9/5/2017 21:51	58	11/5/2017 22:56	56		
3/5/2017 21:36	57	5/5/2017 22:41	57	7/5/2017 11:46	58	7/5/2017 20:51	57	9/5/2017 21:56	57	12/5/2017 19:01	62		
3/5/2017 21:41	57	5/5/2017 22:46	57	7/5/2017 11:51	58	7/5/2017 20:56	56	9/5/2017 22:01	56	12/5/2017 19:06	61		
3/5/2017 21:46	57	5/5/2017 22:51	57	7/5/2017 11:56	59	7/5/2017 21:01	57	9/5/2017 22:06	57	12/5/2017 19:11	60		
3/5/2017 21:51	58	5/5/2017 22:56	58	7/5/2017 12:01	58	7/5/2017 21:06	58	9/5/2017 22:11	56	12/5/2017 19:16	60		
3/5/2017 21:56	57	6/5/2017 19:01	61	7/5/2017 12:06	58	7/5/2017 21:11	58	9/5/2017 22:16	56	12/5/2017 19:21	58		
3/5/2017 22:01	57	6/5/2017 19:06	58	7/5/2017 12:11	58	7/5/2017 21:16	58	9/5/2017 22:21	57	12/5/2017 19:26	58		
3/5/2017 22:06	58	6/5/2017 19:11	57	7/5/2017 12:16	58	7/5/2017 21:21	58	9/5/2017 22:26	57	12/5/2017 19:31	58		
3/5/2017 22:11	61	6/5/2017 19:16	56	7/5/2017 12:21	58	7/5/2017 21:26	58	9/5/2017 22:31	57	12/5/2017 19:36	59		
3/5/2017 22:16	58	6/5/2017 19:21	58	7/5/2017 12:26	59	7/5/2017 21:31	58	9/5/2017 22:36	57	12/5/2017 19:41	58		
3/5/2017 22:21	58	6/5/2017 19:26	59	7/5/2017 12:31	57	7/5/2017 21:36	56	9/5/2017 22:41	57	12/5/2017 19:46	59		
3/5/2017 22:26	60	6/5/2017 19:31	58	7/5/2017 12:36	58	7/5/2017 21:41	57	9/5/2017 22:46	60	12/5/2017 19:51	57		
3/5/2017 22:31	57	6/5/2017 19:36	59	7/5/2017 12:41	58	7/5/2017 21:46	59	9/5/2017 22:51	56	12/5/2017 19:56	57		
3/5/2017 22:36	58	6/5/2017 19:41	57	7/5/2017 12:46	60	7/5/2017 21:51	57	9/5/2017 22:56	56	12/5/2017 20:01	57		
3/5/2017 22:41	57	6/5/2017 19:46	58	7/5/2017 12:51	58	7/5/2017 21:56	57	10/5/2017 19:01	59	12/5/2017 20:06	57		
3/5/2017 22:46	61	6/5/2017 19:51	57	7/5/2017 12:56	58	7/5/2017 22:01	57	10/5/2017 19:06	58	12/5/2017 20:11	59		
3/5/2017 22:51	59	6/5/2017 19:56	59	7/5/2017 13:01	59	7/5/2017 22:06	58	10/5/2017 19:11	60	12/5/2017 20:16	59		
3/5/2017 22:56	57	6/5/2017 20:01	57	7/5/2017 13:06	57	7/5/2017 22:11	56	10/5/2017 19:16	58	12/5/2017 20:21	58		
4/5/2017 19:01	58	6/5/2017 20:06	56	7/5/2017 13:11	59	7/5/2017 22:16	57	10/5/2017 19:21	58	12/5/2017 20:26	58		
4/5/2017 19:06	58	6/5/2017 20:11	56	7/5/2017 13:16	58	7/5/2017 22:21	57	10/5/2017 19:26	59	12/5/2017 20:31	58		
4/5/2017 19:11	57	6/5/2017 20:16	58	7/5/2017 13:21	59	7/5/2017 22:26	58	10/5/2017 19:31	58	12/5/2017 20:36	58		
4/5/2017 19:16	57	6/5/2017 20:21	57	7/5/2017 13:26	58	7/5/2017 22:31	57	10/5/2017 19:36	59	12/5/2017 20:41	57		
4/5/2017 19:21	57	6/5/2017 20:26	59	7/5/2017 13:31	59	7/5/2017 22:36	57	10/5/2017 19:41	58	12/5/2017 20:46	57		
4/5/2017 19:26	58	6/5/2017 20:31	58	7/5/2017 13:36	59	7/5/2017 22:41	56	10/5/2017 19:46	58	12/5/2017 20:51	57		
4/5/2017 19:31	58	6/5/2017 20:36	59	7/5/2017 13:41	53	7/5/2017 22:46	57	10/5/2017 19:51	57	12/5/2017 20:56	58		
4/5/2017 19:36	59	6/5/2017 20:41	58	7/5/2017 13:46	59	7/5/2017 22:51	57	10/5/2017 19:56	59	12/5/2017 21:01	59		
4/5/2017 19:41	58	6/5/2017 20:46	58	7/5/2017 13:51	61	7/5/2017 22:56	56	10/5/2017 20:01	57	12/5/2017 21:06	57		
4/5/2017 19:46	58	6/5/2017 20:51	58	7/5/2017 13:56	59	8/5/2017 19:01	62	10/5/2017 20:06	59	12/5/2017 21:11	56		
4/5/2017 19:51	58	6/5/2017 20:56	57	7/5/2017 14:01	58	8/5/2017 19:06	59	10/5/2017 20:11	58	12/5/2017 21:16	57		
4/5/2017 19:56	58	6/5/2017 21:01	58	7/5/2017 14:06	58	8/5/2017 19:11	63	10/5/2017 20:16	62	12/5/2017 21:21	56		
4/5/2017 20:01	58	6/5/2017 21:06	59	7/5/2017 14:11	58	8/5/2017 19:16	61	10/5/2017 20:21	59	12/5/2017 21:26	57		
4/5/2017 20:06	58	6/5/2017 21:11	60	7/5/2017 14:16	58	8/5/2017 19:21	62	10/5/2017 20:26	60	12/5/2017 21:31	57		
4/5/2017 20:11	58	6/5/2017 21:16	59	7/5/2017 14:21	58	8/5/2017 19:26	58	10/5/2017 20:31	58	12/5/2017 21:36	57		
4/5/2017 20:16	58	6/5/2017 21:21	57	7/5/2017 14:26	58	8/5/2017 19:31	59	10/5/2017 20:36	59	12/5/2017 21:41	57		
4/5/2017 20:21	59	6/5/2017 21:26	58	7/5/2017 14:31	58	8/5/2017 19:36	61	10/5/2017 20:41	58	12/5/2017 21:46	57		
4/5/2017 20:26	57	6/5/2017 21:31	57	7/5/2017 14:36	59	8/5/2017 19:41	59	10/5/2017 20:46	59	12/5/2017 21:51	57		
4/5/2017 20:31	59	6/5/2017 21:36	57	7/5/2017 14:41	58	8/5/2017 19:46	60	10/5/2017 20:51	57	12/5/2017 21:56	57		
4/5/2017 20:36	57	6/5/2017 21:41	58	7/5/2017 14:46	59	8/5/2017 19:51	59	10/5/2017 20:56	57	12/5/2017 22:01	58		
4/5/2017 20:41	58	6/5/2017 21:46	57	7/5/2017 14:51	57	8/5/2017 19:56	59	10/5/2017 21:01	58	12/5/2017 22:06	57		
4/5/2017 20:46	57	6/5/2017 21:51	57	7/5/2017 14:56	57	8/5/2017 20:01	58	10/5/2017 21:06	57	12/5/2017 22:11	60		
4/5/2017 20:51	56	6/5/2017 21:56	60	7/5/2017 15:01	58	8/5/2017 20:06	59	10/5/2017 21:11	57	12/5/2017 22:16	58		
4/5/2017 20:56	56	6/5/2017 22:01	49	7/5/2017 15:06	59	8/5/2017 20:11	59	10/5/2017 21:16	57	12/5/2017 22:21	57		
4/5/2017 21:01	57	6/5/2017 22:06	58	7/5/2017 15:11	58	8/5/2017 20:16	59	10/5/2017 21:21	57	12/5/2017 22:26	57		
4/5/2017 21:06	56	6/5/2017 22:11	59	7/5/2017 15:16	58	8/5/2017 20:21	59	10/5/2017 21:26	56	12/5/2017 22:31	58		
4/5/2017 21:11	56	6/5/2017 22:16	59	7/5/2017 15:21	59	8/5/2017 20:26	60	10/5/2017 21:31	57	12/5/2017 22:36	60		
4/5/2017 21:16	56	6/5/2017 22:21	58	7/5/2017 15:26	58	8/5/2017 20:31	59	10/5/2017 21:36	56	12/5/2017 22:41	57		
4/5/2017 21:21	57	6/5/2017 22:26	57	7/5/2017 15:31	57	8/5/2017 20:36	58	10/5/2017 21:41	57	12/5/2017 22:46	57		
4/5/2017 21:26	57	6/5/2017 22:31	58	7/5/2017 15:36	59								

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
13/5/2017 22:01	59	14/5/2017 15:06	59	15/5/2017 20:11	58	17/5/2017 21:16	57	19/5/2017 22:21	56	21/5/2017 11:26	58
13/5/2017 22:06	59	14/5/2017 15:11	57	15/5/2017 20:16	58	17/5/2017 21:21	56	19/5/2017 22:26	58	21/5/2017 11:31	58
13/5/2017 22:11	58	14/5/2017 15:16	58	15/5/2017 20:21	57	17/5/2017 21:26	56	19/5/2017 22:31	56	21/5/2017 11:36	60
13/5/2017 22:16	59	14/5/2017 15:21	58	15/5/2017 20:26	58	17/5/2017 21:31	57	19/5/2017 22:36	57	21/5/2017 11:41	58
13/5/2017 22:21	57	14/5/2017 15:26	58	15/5/2017 20:31	58	17/5/2017 21:36	56	19/5/2017 22:41	56	21/5/2017 11:46	59
13/5/2017 22:26	60	14/5/2017 15:31	57	15/5/2017 20:36	57	17/5/2017 21:41	56	19/5/2017 22:46	56	21/5/2017 11:51	57
13/5/2017 22:31	58	14/5/2017 15:36	58	15/5/2017 20:41	57	17/5/2017 21:46	56	19/5/2017 22:51	57	21/5/2017 11:56	58
13/5/2017 22:36	59	14/5/2017 15:41	58	15/5/2017 20:46	57	17/5/2017 21:51	58	19/5/2017 22:56	56	21/5/2017 12:01	58
13/5/2017 22:41	57	14/5/2017 15:46	59	15/5/2017 20:51	57	17/5/2017 21:56	57	20/5/2017 19:01	60	21/5/2017 12:06	58
13/5/2017 22:46	57	14/5/2017 15:51	52	15/5/2017 20:56	57	17/5/2017 22:01	58	20/5/2017 19:06	58	21/5/2017 12:11	59
13/5/2017 22:51	58	14/5/2017 15:56	58	15/5/2017 21:01	57	17/5/2017 22:06	59	20/5/2017 19:11	57	21/5/2017 12:16	57
13/5/2017 22:56	57	14/5/2017 16:01	58	15/5/2017 21:06	59	17/5/2017 22:11	57	20/5/2017 19:16	58	21/5/2017 12:21	57
14/5/2017 7:01	55	14/5/2017 16:06	58	15/5/2017 21:11	58	17/5/2017 22:16	61	20/5/2017 19:21	59	21/5/2017 12:26	57
14/5/2017 7:06	55	14/5/2017 16:11	58	15/5/2017 21:16	58	17/5/2017 22:21	58	20/5/2017 19:26	58	21/5/2017 12:31	58
14/5/2017 7:11	55	14/5/2017 16:16	58	15/5/2017 21:21	57	17/5/2017 22:26	57	20/5/2017 19:31	59	21/5/2017 12:36	57
14/5/2017 7:16	58	14/5/2017 16:21	59	15/5/2017 21:26	57	17/5/2017 22:31	60	20/5/2017 19:36	58	21/5/2017 12:41	58
14/5/2017 7:21	55	14/5/2017 16:26	59	15/5/2017 21:31	59	17/5/2017 22:36	60	20/5/2017 19:41	59	21/5/2017 12:46	58
14/5/2017 7:26	55	14/5/2017 16:31	60	15/5/2017 21:36	57	17/5/2017 22:41	56	20/5/2017 19:46	58	21/5/2017 12:51	58
14/5/2017 7:31	58	14/5/2017 16:36	59	15/5/2017 21:41	59	17/5/2017 22:46	57	20/5/2017 19:51	57	21/5/2017 12:56	61
14/5/2017 7:36	61	14/5/2017 16:41	59	15/5/2017 21:46	60	17/5/2017 22:51	57	20/5/2017 19:56	57	21/5/2017 13:01	58
14/5/2017 7:41	61	14/5/2017 16:46	58	15/5/2017 21:51	57	17/5/2017 22:56	57	20/5/2017 20:01	52	21/5/2017 13:06	58
14/5/2017 7:46	57	14/5/2017 16:51	60	15/5/2017 21:56	58	18/5/2017 19:01	59	20/5/2017 20:06	62	21/5/2017 13:11	57
14/5/2017 7:51	56	14/5/2017 16:56	59	15/5/2017 22:01	52	18/5/2017 19:06	59	20/5/2017 20:11	59	21/5/2017 13:16	59
14/5/2017 7:56	56	14/5/2017 17:01	60	15/5/2017 22:06	57	18/5/2017 19:11	58	20/5/2017 20:16	57	21/5/2017 13:21	57
14/5/2017 8:01	57	14/5/2017 17:06	59	15/5/2017 22:11	58	18/5/2017 19:16	58	20/5/2017 20:21	58	21/5/2017 13:26	58
14/5/2017 8:06	58	14/5/2017 17:11	62	15/5/2017 22:16	59	18/5/2017 19:21	57	20/5/2017 20:26	57	21/5/2017 13:31	58
14/5/2017 8:11	61	14/5/2017 17:16	58	15/5/2017 22:21	57	18/5/2017 19:26	58	20/5/2017 20:31	57	21/5/2017 13:36	58
14/5/2017 8:16	57	14/5/2017 17:21	59	15/5/2017 22:26	57	18/5/2017 19:31	58	20/5/2017 20:36	58	21/5/2017 13:41	58
14/5/2017 8:21	58	14/5/2017 17:26	58	15/5/2017 22:31	57	18/5/2017 19:36	58	20/5/2017 20:41	59	21/5/2017 13:46	57
14/5/2017 8:26	57	14/5/2017 17:31	58	15/5/2017 22:36	57	18/5/2017 19:41	59	20/5/2017 20:46	59	21/5/2017 13:51	58
14/5/2017 8:31	58	14/5/2017 17:36	60	15/5/2017 22:41	58	18/5/2017 19:46	62	20/5/2017 20:51	58	21/5/2017 13:56	57
14/5/2017 8:36	57	14/5/2017 17:41	59	15/5/2017 22:46	56	18/5/2017 19:51	57	20/5/2017 20:56	58	21/5/2017 14:01	58
14/5/2017 8:41	57	14/5/2017 17:46	59	15/5/2017 22:51	58	18/5/2017 19:56	60	20/5/2017 21:01	58	21/5/2017 14:06	57
14/5/2017 8:46	57	14/5/2017 17:51	58	15/5/2017 22:56	58	18/5/2017 20:01	58	20/5/2017 21:06	56	21/5/2017 14:11	59
14/5/2017 8:51	58	14/5/2017 17:56	58	16/5/2017 19:01	57	18/5/2017 20:06	58	20/5/2017 21:11	57	21/5/2017 14:16	58
14/5/2017 8:56	57	14/5/2017 18:01	60	16/5/2017 19:06	59	18/5/2017 20:11	58	20/5/2017 21:16	56	21/5/2017 14:21	59
14/5/2017 9:01	58	14/5/2017 18:06	59	16/5/2017 19:11	58	18/5/2017 20:16	59	20/5/2017 21:21	56	21/5/2017 14:26	58
14/5/2017 9:06	59	14/5/2017 18:11	60	16/5/2017 19:16	58	18/5/2017 20:21	57	20/5/2017 21:26	59	21/5/2017 14:31	58
14/5/2017 9:11	57	14/5/2017 18:16	61	16/5/2017 19:21	58	18/5/2017 20:26	57	20/5/2017 21:31	56	21/5/2017 14:36	58
14/5/2017 9:16	58	14/5/2017 18:21	59	16/5/2017 19:26	57	18/5/2017 20:31	59	20/5/2017 21:36	62	21/5/2017 14:41	58
14/5/2017 9:21	57	14/5/2017 18:26	59	16/5/2017 19:31	58	18/5/2017 20:36	59	20/5/2017 21:41	58	21/5/2017 14:46	58
14/5/2017 9:26	57	14/5/2017 18:31	59	16/5/2017 19:36	58	18/5/2017 20:41	57	20/5/2017 21:46	56	21/5/2017 14:51	58
14/5/2017 9:31	57	14/5/2017 18:36	59	16/5/2017 19:41	58	18/5/2017 20:46	58	20/5/2017 21:51	60	21/5/2017 14:56	58
14/5/2017 9:36	60	14/5/2017 18:41	59	16/5/2017 19:46	57	18/5/2017 20:51	59	20/5/2017 21:56	58	21/5/2017 15:01	58
14/5/2017 9:41	59	14/5/2017 18:46	59	16/5/2017 19:51	59	18/5/2017 20:56	58	20/5/2017 22:01	58	21/5/2017 15:06	59
14/5/2017 9:46	58	14/5/2017 18:51	58	16/5/2017 19:56	59	18/5/2017 21:01	58	20/5/2017 22:06	56	21/5/2017 15:11	57
14/5/2017 9:51	58	14/5/2017 18:56	57	16/5/2017 20:01	53	18/5/2017 21:06	60	20/5/2017 22:11	57	21/5/2017 15:16	58
14/5/2017 9:56	58	14/5/2017 19:01	58	16/5/2017 20:06	58	18/5/2017 21:11	60	20/5/2017 22:16	57	21/5/2017 15:21	58
14/5/2017 10:01	59	14/5/2017 19:06	62	16/5/2017 20:11	58	18/5/2017 21:16	57	20/5/2017 22:21	57	21/5/2017 15:26	59
14/5/2017 10:06	59	14/5/2017 19:11	57	16/5/2017 20:16	58	18/5/2017 21:21	58	20/5/2017 22:26	56	21/5/2017 15:31	58
14/5/2017 10:11	59	14/5/2017 19:16	57	16/5/2017 20:21	48	18/5/2017 21:26	57	20/5/2017 22:31	56	21/5/2017 15:36	58
14/5/2017 10:16	58	14/5/2017 19:21	59	16/5/2017 20:26	59	18/5/2017 21:31	57	20/5/2017 22:36	57	21/5/2017 15:41	57
14/5/2017 10:21	58	14/5/2017 19:26	58	16/5/2017 20:31	58	18/5/2017 21:36	58	20/5/2017 22:41	57	21/5/2017 15:46	58
14/5/2017 10:26	58	14/5/2017 19:31	59	16/5/2017 20:36	58	18/5/2017 21:41	58	20/5/2017 22:46	57	21/5/2017 15:51	58
14/5/2017 10:31	58	14/5/2017 19:36	58	16/5/2017 20:41	57	18/5/2017 21:46	58	20/5/2017 22:51	57	21/5/2017 15:56	58
14/5/2017 10:36	58	14/5/2017 19:41	59	16/5/2017 20:46	58	18/5/2017 21:51	60	20/5/2017 22:56	57	21/5/2017 16:01	57
14/5/2017 10:41	58	14/5/2017 19:46	59	16/5/2017 20:51	58	18/5/2017 21:56	57	21/5/2017 7:01	56	21/5/2017 16:06	57
14/5/2017 10:46	59	14/5/2017 19:51	58	16/5/2017 20:56	56	18/5/2017 22:01	58	21/5/2017 7:06	58	21/5/2017 16:11	59
14/5/2017 10:51	57	14/5/2017 19:56	58	16/5/2017 21:01	58	18/5/2017 22:06	57	21/5/2017 7:11	59	21/5/2017 16:16	59
14/5/2017 10:56	59	14/5/2017 20:01	58	16/5/2017 21:06	59	18/5/2017 22:11	57	21/5/2017 7:16	60	21/5/2017 16:21	57
14/5/2017 11:01	56	14/5/2017 20:06	58	16/5/2017 21:11	58	18/5/2017 22:16	57	21/5/2017 7:21	57	21/5/2017 16:26	58
14/5/2017 11:06	57	14/5/2017 20:11	58	16/5/2017 21:16	60	18/5/2017 22:21	57	21/5/2017 7:26	58	21/5/2017 16:31	62
14/5/2017 11:11	59	14/5/2017 20:16	58	16/5/2017 21:21	56	18/5/2017 22:26	58	21/5/2017 7:31	56	21/5/2017 16:36	58
14/5/2017 11:16	58	14/5/2017 20:21	58	16/5/2017 21:26	56	18/5/2017 22:31	58	21/5/2017 7:36	56	21/5/2017 16:41	58
14/5/2017 11:21	58	14/5/2017 20:26	60	16/5/2017 21:31	57	18/5/2017 22:36	57	21/5/2017 7:41	57	21/5/2017 16:46	59
14/5/2017 11:26	57	14/5/2017 20:31	58	16/5/2017 21:36	57	18/5/2017 22:41	58	21/5/2017 7:46	56	21/5/2017 16:51	58
14/5/2017 11:31	59	14/5/2017 20:36	57	16/5/2017 21:41	57	18/5/2017 22:46	58	21/5/2017 7:51	56	21/5/2017 16:56	58
14/5/2017 11:36	59	14/5/2017 20:41	59	16/5/2017 21:46	58	18/5/2017 22:51	57	21/5/2017 7:56	57	21/5/2017 17:01	57
14/5/2017 11:41	58	14/5/2017 20:46	59	16/5/2017 21:51	58	18/5/2017 22:56	56	21/5/2017 8:01	57	21/5/2017 17:06	58
14/5/2017 11:46	59	14/5/2017 20:51	58	16/5/2017 21:56	60	19/5/2017 19:01	59	21/5/2017 8:06	57	21/5/2017 17:11	57
14/5/2017 11:51	58	14/5/2017 20:56	57	16/5/2017 22:01	58	19/5/2017 19:06	58	21/5/2017 8:11	58	21/5/2017 17:16	57
14/5/2017 11:56	58	14/5/2017 21:01	56	16/5/2017 22:06	57	19/5/2017 19:11	58	21/5/2017 8:16	57	21/5/2017 17:21	58
14/5/2017 12:01	58	14/5/2017 21:06	57	16/5/2017 22:11	59	19/5/2017 19:16	59	21/5/2017 8:21	58	21/5/2017 17:26	58
14/5/2017 12:06	58	14/5/2017 21:11	57	16/5/2017 22:16	58	19/5/2017 19:21	57	21/5/2017 8:26	56	21/5/2017 17:31	58

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)													
21/5/2017 20:31	57	23/5/2017 21:36	59	25/5/2017 22:41	59	27/4/2017 4:31	52	28/4/2017 5:36	52	29/4/2017 6:41	58				
21/5/2017 20:36	57	23/5/2017 21:41	60	25/5/2017 22:46	58	27/4/2017 4:36	53	28/4/2017 5:41	54	29/4/2017 6:46	55				
21/5/2017 20:41	56	23/5/2017 21:46	57	25/5/2017 22:51	58	27/4/2017 4:41	52	28/4/2017 5:46	54	29/4/2017 6:51	56				
21/5/2017 20:46	59	23/5/2017 21:51	58	25/5/2017 22:56	57	27/4/2017 4:46	53	28/4/2017 5:51	53	29/4/2017 6:56	57				
21/5/2017 20:51	56	23/5/2017 21:56	57	26/5/2017 19:01	58	27/4/2017 4:51	54	28/4/2017 5:56	53	29/4/2017 23:01	58				
21/5/2017 20:56	58	23/5/2017 22:01	57	26/5/2017 19:06	57	27/4/2017 4:56	55	28/4/2017 6:01	55	29/4/2017 23:06	57				
21/5/2017 21:01	57	23/5/2017 22:06	58	26/5/2017 19:11	59	27/4/2017 5:01	54	28/4/2017 6:06	54	29/4/2017 23:11	57				
21/5/2017 21:06	57	23/5/2017 22:11	57	26/5/2017 19:16	57	27/4/2017 5:06	56	28/4/2017 6:11	54	29/4/2017 23:16	57				
21/5/2017 21:11	57	23/5/2017 22:16	58	26/5/2017 19:21	58	27/4/2017 5:11	52	28/4/2017 6:16	55	29/4/2017 23:21	56				
21/5/2017 21:16	57	23/5/2017 22:21	58	26/5/2017 19:26	58	27/4/2017 5:16	54	28/4/2017 6:21	54	29/4/2017 23:26	56				
21/5/2017 21:21	58	23/5/2017 22:26	58	26/5/2017 19:31	60	27/4/2017 5:21	54	28/4/2017 6:26	56	29/4/2017 23:31	55				
21/5/2017 21:26	57	23/5/2017 22:31	58	26/5/2017 19:36	50	27/4/2017 5:26	54	28/4/2017 6:31	55	29/4/2017 23:36	55				
21/5/2017 21:31	57	23/5/2017 22:36	58	26/5/2017 19:41	58	27/4/2017 5:31	54	28/4/2017 6:36	55	29/4/2017 23:41	55				
21/5/2017 21:36	57	23/5/2017 22:41	57	26/5/2017 19:46	59	27/4/2017 5:36	53	28/4/2017 6:41	55	29/4/2017 23:46	55				
21/5/2017 21:41	57	23/5/2017 22:46	57	26/5/2017 19:51	58	27/4/2017 5:41	54	28/4/2017 6:46	57	29/4/2017 23:51	56				
21/5/2017 21:46	57	23/5/2017 22:51	60	26/5/2017 19:56	57	27/4/2017 5:46	54	28/4/2017 6:51	56	29/4/2017 23:56	55				
21/5/2017 21:51	57	23/5/2017 22:56	57	26/5/2017 20:01	57	27/4/2017 5:51	53	28/4/2017 6:56	56	30/4/2017 0:01	55				
21/5/2017 21:56	57	24/5/2017 19:01	60	26/5/2017 20:06	59	27/4/2017 5:56	54	28/4/2017 23:01	56	30/4/2017 0:06	55				
21/5/2017 22:01	56	24/5/2017 19:06	59	26/5/2017 20:11	58	27/4/2017 6:01	54	28/4/2017 23:06	56	30/4/2017 0:11	55				
21/5/2017 22:06	59	24/5/2017 19:11	58	26/5/2017 20:16	57	27/4/2017 6:06	55	28/4/2017 23:11	56	30/4/2017 0:16	55				
21/5/2017 22:11	56	24/5/2017 19:16	60	26/5/2017 20:21	59	27/4/2017 6:11	55	28/4/2017 23:16	57	30/4/2017 0:21	55				
21/5/2017 22:16	58	24/5/2017 19:21	59	26/5/2017 20:26	58	27/4/2017 6:16	54	28/4/2017 23:21	51	30/4/2017 0:26	55				
21/5/2017 22:21	56	24/5/2017 19:26	59	26/5/2017 20:31	58	27/4/2017 6:21	54	28/4/2017 23:26	56	30/4/2017 0:31	55				
21/5/2017 22:26	57	24/5/2017 19:31	58	26/5/2017 20:36	57	27/4/2017 6:26	55	28/4/2017 23:31	58	30/4/2017 0:36	55				
21/5/2017 22:31	56	24/5/2017 19:36	58	26/5/2017 20:41	57	27/4/2017 6:31	55	28/4/2017 23:36	56	30/4/2017 0:41	55				
21/5/2017 22:36	56	24/5/2017 19:41	58	26/5/2017 20:46	58	27/4/2017 6:36	56	28/4/2017 23:41	56	30/4/2017 0:46	54				
21/5/2017 22:41	56	24/5/2017 19:46	55	26/5/2017 20:51	59	27/4/2017 6:41	56	28/4/2017 23:46	56	30/4/2017 0:51	56				
21/5/2017 22:46	58	24/5/2017 19:51	59	26/5/2017 20:56	58	27/4/2017 6:46	56	28/4/2017 23:51	57	30/4/2017 0:56	55				
21/5/2017 22:51	57	24/5/2017 19:56	58	26/5/2017 21:01	57	27/4/2017 6:51	56	28/4/2017 23:56	56	30/4/2017 1:01	55				
21/5/2017 22:56	55	24/5/2017 20:01	54	26/5/2017 21:06	57	27/4/2017 6:56	57	29/4/2017 0:01	56	30/4/2017 1:06	55				
22/5/2017 19:01	57	24/5/2017 20:06	57	26/5/2017 21:11	56	27/4/2017 23:01	54	29/4/2017 0:06	55	30/4/2017 1:11	55				
22/5/2017 19:06	59	24/5/2017 20:11	58	26/5/2017 21:16	56	27/4/2017 23:06	57	29/4/2017 0:11	55	30/4/2017 1:16	54				
22/5/2017 19:11	58	24/5/2017 20:16	58	26/5/2017 21:21	59	27/4/2017 23:11	56	29/4/2017 0:16	55	30/4/2017 1:21	54				
22/5/2017 19:16	58	24/5/2017 20:21	57	26/5/2017 21:26	57	27/4/2017 23:16	57	29/4/2017 0:21	56	30/4/2017 1:26	54				
22/5/2017 19:21	57	24/5/2017 20:26	57	26/5/2017 21:31	57	27/4/2017 23:21	52	29/4/2017 0:26	55	30/4/2017 1:31	54				
22/5/2017 19:26	57	24/5/2017 20:31	57	26/5/2017 21:36	56	27/4/2017 23:26	55	29/4/2017 0:31	55	30/4/2017 1:36	53				
22/5/2017 19:31	56	24/5/2017 20:36	59	26/5/2017 21:41	57	27/4/2017 23:31	55	29/4/2017 0:36	55	30/4/2017 1:41	54				
22/5/2017 19:36	57	24/5/2017 20:41	61	26/5/2017 21:46	57	27/4/2017 23:36	56	29/4/2017 0:41	55	30/4/2017 1:46	54				
22/5/2017 19:41	59	24/5/2017 20:46	57	26/5/2017 21:51	44	27/4/2017 23:41	56	29/4/2017 0:46	56	30/4/2017 1:51	54				
22/5/2017 19:46	57	24/5/2017 20:51	57	26/5/2017 21:56	59	27/4/2017 23:46	55	29/4/2017 0:51	56	30/4/2017 1:56	54				
22/5/2017 19:51	57	24/5/2017 20:56	60	26/5/2017 22:01	57	27/4/2017 23:51	55	29/4/2017 0:56	56	30/4/2017 2:01	56				
22/5/2017 19:56	57	24/5/2017 21:01	57	26/5/2017 22:06	57	27/4/2017 23:56	55	29/4/2017 1:01	55	30/4/2017 2:06	54				
22/5/2017 20:01	58	24/5/2017 21:06	57	26/5/2017 22:11	58	28/4/2017 0:01	55	29/4/2017 1:06	55	30/4/2017 2:11	54				
22/5/2017 20:06	57	24/5/2017 21:11	59	26/5/2017 22:16	57	28/4/2017 0:06	56	29/4/2017 1:11	54	30/4/2017 2:16	53				
22/5/2017 20:11	57	24/5/2017 21:16	58	26/5/2017 22:21	57	28/4/2017 0:11	56	29/4/2017 1:16	55	30/4/2017 2:21	55				
22/5/2017 20:16	57	24/5/2017 21:21	57	26/5/2017 22:26	60	28/4/2017 0:16	55	29/4/2017 1:21	57	30/4/2017 2:26	54				
22/5/2017 20:21	56	24/5/2017 21:26	59	26/5/2017 22:31	58	28/4/2017 0:21	55	29/4/2017 1:26	55	30/4/2017 2:31	53				
22/5/2017 20:26	57	24/5/2017 21:31	58	26/5/2017 22:36	58	28/4/2017 0:26	56	29/4/2017 1:31	55	30/4/2017 2:36	54				
22/5/2017 20:31	57	24/5/2017 21:36	59	26/5/2017 22:41	59	28/4/2017 0:31	55	29/4/2017 1:36	55	30/4/2017 2:41	54				
22/5/2017 20:36	56	24/5/2017 21:41	57	26/5/2017 22:46	59	28/4/2017 0:36	55	29/4/2017 1:41	54	30/4/2017 2:46	54				
22/5/2017 20:41	56	24/5/2017 21:46	57	26/5/2017 22:51	59	28/4/2017 0:41	56	29/4/2017 1:46	55	30/4/2017 2:51	53				
22/5/2017 20:46	56	24/5/2017 21:51	57	26/5/2017 22:56	58	28/4/2017 0:46	55	29/4/2017 1:51	55	30/4/2017 2:56	53				
22/5/2017 20:51	56	24/5/2017 21:56	57	25/5/2017 19:01	59	28/4/2017 0:51	54	29/4/2017 1:56	54	30/4/2017 3:01	53				
22/5/2017 20:56	56	24/5/2017 22:01	56	25/5/2017 19:06	58	28/4/2017 0:56	55	29/4/2017 2:01	54	30/4/2017 3:06	54				
22/5/2017 21:01	56	24/5/2017 22:06	56	25/5/2017 19:11	43	28/4/2017 1:01	54	29/4/2017 2:06	54	30/4/2017 3:11	53				
22/5/2017 21:06	56	24/5/2017 22:11	57	25/5/2017 19:16	59	28/4/2017 1:06	54	29/4/2017 2:11	54	30/4/2017 3:16	53				
22/5/2017 21:11	58	24/5/2017 22:16	56	25/5/2017 19:21	58	28/4/2017 1:11	55	29/4/2017 2:16	54	30/4/2017 3:21	53				
22/5/2017 21:16	57	24/5/2017 22:21	56	25/5/2017 19:26	58	28/4/2017 1:16	54	29/4/2017 2:21	53	30/4/2017 3:26	54				
22/5/2017 21:21	56	24/5/2017 22:26	57	25/5/2017 19:31	62	28/4/2017 1:21	55	29/4/2017 2:26	55	30/4/2017 3:31	53				
22/5/2017 21:26	56	24/5/2017 22:31	57	25/5/2017 19:36	62	28/4/2017 1:26	54	29/4/2017 2:31	53	30/4/2017 3:36	53				
22/5/2017 21:31	55	24/5/2017 22:36	57	25/5/2017 19:41	60	28/4/2017 1:31	54	29/4/2017 2:36	54	30/4/2017 3:41	52				
22/5/2017 21:36	56	24/5/2017 22:41	56	25/5/2017 19:46	59	28/4/2017 1:36	54	29/4/2017 2:41	55	30/4/2017 3:46	53				
22/5/2017 21:41	56	24/5/2017 22:46	56	25/5/2017 19:51	59	28/4/2017 1:41	53	29/4/2017 2:46	56	30/4/2017 3:51	53				
22/5/2017 21:46	58	24/5/2017 22:51	56	25/5/2017 19:56	58	28/4/2017 1:46	54	29/4/2017 2:51	54	30/4/2017 3:56	53				
22/5/2017 21:51	57	24/5/2017 22:56	56	25/5/2017 20:01	61	28/4/2017 1:51	54	29/4/2017 2:56	54	30/4/2017 4:01	52				
22/5/2017 21:56	58	25/5/2017 19:01	59	25/5/2017 20:06	61	28/4/2017 1:56	53	29/4/2017 3:01	54	30/4/2017 4:06	53				
22/5/2017 22:01	56	25/5/2017 19:06	58	25/5/2017 20:11	58	28/4/2017 2:01	55	29/4/2017 3:06	54	30/4/2017 4:11	52				
22/5/2017 22:06	56	25/5/2017 19:11	43	25/5/2017 20:16	59										

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)											
30/4/2017 23:46	58	2/5/2017 0:51	54	3/5/2017 1:56	55	4/5/2017 3:01	55	5/5/2017 4:06	53	6/5/2017 5:11	54		
30/4/2017 23:51	55	2/5/2017 0:56	53	3/5/2017 2:01	55	4/5/2017 3:06	54	5/5/2017 4:11	54	6/5/2017 5:16	55		
30/4/2017 23:56	56	2/5/2017 1:01	54	3/5/2017 2:06	55	4/5/2017 3:11	53	5/5/2017 4:16	54	6/5/2017 5:21	55		
1/5/2017 0:01	54	2/5/2017 1:06	54	3/5/2017 2:11	55	4/5/2017 3:16	53	5/5/2017 4:21	54	6/5/2017 5:26	55		
1/5/2017 0:06	55	2/5/2017 1:11	53	3/5/2017 2:16	54	4/5/2017 3:21	54	5/5/2017 4:26	55	6/5/2017 5:31	55		
1/5/2017 0:11	55	2/5/2017 1:16	53	3/5/2017 2:21	54	4/5/2017 3:26	54	5/5/2017 4:31	54	6/5/2017 5:36	55		
1/5/2017 0:16	55	2/5/2017 1:21	53	3/5/2017 2:26	55	4/5/2017 3:31	54	5/5/2017 4:36	55	6/5/2017 5:41	54		
1/5/2017 0:21	55	2/5/2017 1:26	53	3/5/2017 2:31	55	4/5/2017 3:36	54	5/5/2017 4:41	54	6/5/2017 5:46	55		
1/5/2017 0:26	54	2/5/2017 1:31	54	3/5/2017 2:36	55	4/5/2017 3:41	54	5/5/2017 4:46	54	6/5/2017 5:51	54		
1/5/2017 0:31	55	2/5/2017 1:36	53	3/5/2017 2:41	54	4/5/2017 3:46	54	5/5/2017 4:51	53	6/5/2017 5:56	54		
1/5/2017 0:36	54	2/5/2017 1:41	53	3/5/2017 2:46	57	4/5/2017 3:51	55	5/5/2017 4:56	54	6/5/2017 6:01	54		
1/5/2017 0:41	54	2/5/2017 1:46	53	3/5/2017 2:51	54	4/5/2017 3:56	54	5/5/2017 5:01	54	6/5/2017 6:06	54		
1/5/2017 0:46	55	2/5/2017 1:51	53	3/5/2017 2:56	55	4/5/2017 4:01	54	5/5/2017 5:06	54	6/5/2017 6:11	56		
1/5/2017 0:51	54	2/5/2017 1:56	53	3/5/2017 3:01	54	4/5/2017 4:06	54	5/5/2017 5:11	53	6/5/2017 6:16	55		
1/5/2017 0:56	54	2/5/2017 2:01	52	3/5/2017 3:06	54	4/5/2017 4:11	55	5/5/2017 5:16	54	6/5/2017 6:21	55		
1/5/2017 1:01	54	2/5/2017 2:06	53	3/5/2017 3:11	54	4/5/2017 4:16	53	5/5/2017 5:21	53	6/5/2017 6:26	56		
1/5/2017 1:06	54	2/5/2017 2:11	52	3/5/2017 3:16	57	4/5/2017 4:21	53	5/5/2017 5:26	54	6/5/2017 6:31	56		
1/5/2017 1:11	54	2/5/2017 2:16	53	3/5/2017 3:21	54	4/5/2017 4:26	54	5/5/2017 5:31	54	6/5/2017 6:36	57		
1/5/2017 1:16	54	2/5/2017 2:21	53	3/5/2017 3:26	53	4/5/2017 4:31	55	5/5/2017 5:36	54	6/5/2017 6:41	55		
1/5/2017 1:21	54	2/5/2017 2:26	53	3/5/2017 3:31	53	4/5/2017 4:36	55	5/5/2017 5:41	53	6/5/2017 6:46	56		
1/5/2017 1:26	55	2/5/2017 2:31	55	3/5/2017 3:36	54	4/5/2017 4:41	54	5/5/2017 5:46	54	6/5/2017 6:51	57		
1/5/2017 1:31	53	2/5/2017 2:36	55	3/5/2017 3:41	54	4/5/2017 4:46	55	5/5/2017 5:51	54	6/5/2017 6:56	56		
1/5/2017 1:36	54	2/5/2017 2:41	52	3/5/2017 3:46	55	4/5/2017 4:51	55	5/5/2017 5:56	55	6/5/2017 7:01	56		
1/5/2017 1:41	54	2/5/2017 2:46	53	3/5/2017 3:51	55	4/5/2017 4:56	53	5/5/2017 6:01	55	6/5/2017 7:06	57		
1/5/2017 1:46	53	2/5/2017 2:51	54	3/5/2017 3:56	55	4/5/2017 5:01	56	5/5/2017 6:06	54	6/5/2017 7:11	58		
1/5/2017 1:51	54	2/5/2017 2:56	53	3/5/2017 4:01	54	4/5/2017 5:06	53	5/5/2017 6:11	54	6/5/2017 7:16	57		
1/5/2017 1:56	53	2/5/2017 3:01	52	3/5/2017 4:06	54	4/5/2017 5:11	52	5/5/2017 6:16	55	6/5/2017 7:21	57		
1/5/2017 2:01	53	2/5/2017 3:06	57	3/5/2017 4:11	54	4/5/2017 5:16	52	5/5/2017 6:21	57	6/5/2017 7:26	56		
1/5/2017 2:06	53	2/5/2017 3:11	52	3/5/2017 4:16	54	4/5/2017 5:21	52	5/5/2017 6:26	56	6/5/2017 7:31	58		
1/5/2017 2:11	53	2/5/2017 3:16	52	3/5/2017 4:21	53	4/5/2017 5:26	53	5/5/2017 6:31	56	6/5/2017 7:36	57		
1/5/2017 2:16	53	2/5/2017 3:21	52	3/5/2017 4:26	54	4/5/2017 5:31	53	5/5/2017 6:36	56	6/5/2017 7:41	57		
1/5/2017 2:21	53	2/5/2017 3:26	53	3/5/2017 4:31	54	4/5/2017 5:36	54	5/5/2017 6:41	56	6/5/2017 7:46	57		
1/5/2017 2:26	53	2/5/2017 3:31	51	3/5/2017 4:36	54	4/5/2017 5:41	55	5/5/2017 6:46	56	6/5/2017 7:51	48		
1/5/2017 2:31	53	2/5/2017 3:36	52	3/5/2017 4:41	53	4/5/2017 5:46	54	5/5/2017 6:51	57	6/5/2017 7:56	56		
1/5/2017 2:36	53	2/5/2017 3:41	53	3/5/2017 4:46	54	4/5/2017 5:51	54	5/5/2017 6:56	57	7/5/2017 0:01	56		
1/5/2017 2:41	54	2/5/2017 3:46	52	3/5/2017 4:51	54	4/5/2017 5:56	54	5/5/2017 7:01	55	7/5/2017 0:06	56		
1/5/2017 2:46	53	2/5/2017 3:51	53	3/5/2017 4:56	53	4/5/2017 6:01	55	5/5/2017 7:06	58	7/5/2017 0:11	57		
1/5/2017 2:51	52	2/5/2017 3:56	52	3/5/2017 5:01	55	4/5/2017 6:06	56	5/5/2017 7:11	57	7/5/2017 0:16	56		
1/5/2017 2:56	53	2/5/2017 4:01	53	3/5/2017 5:06	54	4/5/2017 6:11	56	5/5/2017 7:16	57	7/5/2017 0:21	56		
1/5/2017 3:01	53	2/5/2017 4:06	53	3/5/2017 5:11	54	4/5/2017 6:16	55	5/5/2017 7:21	57	7/5/2017 0:26	56		
1/5/2017 3:06	53	2/5/2017 4:11	54	3/5/2017 5:16	54	4/5/2017 6:21	55	5/5/2017 7:26	57	7/5/2017 0:31	56		
1/5/2017 3:11	52	2/5/2017 4:16	52	3/5/2017 5:21	54	4/5/2017 6:26	56	5/5/2017 7:31	57	7/5/2017 0:36	56		
1/5/2017 3:16	53	2/5/2017 4:21	53	3/5/2017 5:26	54	4/5/2017 6:31	56	5/5/2017 7:36	57	7/5/2017 0:41	56		
1/5/2017 3:21	52	2/5/2017 4:26	52	3/5/2017 5:31	55	4/5/2017 6:36	57	5/5/2017 7:41	56	7/5/2017 0:46	56		
1/5/2017 3:26	52	2/5/2017 4:31	51	3/5/2017 5:36	56	4/5/2017 6:41	57	5/5/2017 7:46	56	7/5/2017 0:51	55		
1/5/2017 3:31	52	2/5/2017 4:36	52	3/5/2017 5:41	56	4/5/2017 6:46	58	5/5/2017 7:51	56	7/5/2017 0:56	55		
1/5/2017 3:36	53	2/5/2017 4:41	53	3/5/2017 5:46	55	4/5/2017 6:51	56	5/5/2017 7:56	57	7/5/2017 1:01	56		
1/5/2017 3:41	52	2/5/2017 4:46	53	3/5/2017 5:51	55	4/5/2017 6:56	56	6/5/2017 0:01	57	7/5/2017 1:06	56		
1/5/2017 3:46	53	2/5/2017 4:51	52	3/5/2017 5:56	55	4/5/2017 7:01	58	6/5/2017 0:06	56	7/5/2017 1:11	55		
1/5/2017 3:51	53	2/5/2017 4:56	53	3/5/2017 6:01	54	4/5/2017 7:06	58	6/5/2017 0:11	56	7/5/2017 1:16	56		
1/5/2017 3:56	52	2/5/2017 5:01	52	3/5/2017 6:06	55	4/5/2017 7:11	58	6/5/2017 0:16	56	7/5/2017 1:21	56		
1/5/2017 4:01	52	2/5/2017 5:06	53	3/5/2017 6:11	55	4/5/2017 7:16	56	6/5/2017 0:21	57	7/5/2017 1:26	56		
1/5/2017 4:06	52	2/5/2017 5:11	54	3/5/2017 6:16	55	4/5/2017 7:21	57	6/5/2017 0:26	56	7/5/2017 1:31	57		
1/5/2017 4:11	53	2/5/2017 5:16	57	3/5/2017 6:21	55	4/5/2017 7:26	57	6/5/2017 0:31	56	7/5/2017 1:36	56		
1/5/2017 4:16	53	2/5/2017 5:21	52	3/5/2017 6:26	56	4/5/2017 7:31	57	6/5/2017 0:36	56	7/5/2017 1:41	50		
1/5/2017 4:21	52	2/5/2017 5:26	53	3/5/2017 6:31	55	4/5/2017 7:36	57	6/5/2017 0:41	56	7/5/2017 1:46	56		
1/5/2017 4:26	53	2/5/2017 5:31	54	3/5/2017 6:36	58	4/5/2017 7:41	55	6/5/2017 0:46	56	7/5/2017 1:51	55		
1/5/2017 4:31	52	2/5/2017 5:36	52	3/5/2017 6:41	55	4/5/2017 7:46	56	6/5/2017 0:51	56	7/5/2017 1:56	55		
1/5/2017 4:36	53	2/5/2017 5:41	55	3/5/2017 6:46	56	4/5/2017 7:51	55	6/5/2017 0:56	55	7/5/2017 2:01	56		
1/5/2017 4:41	52	2/5/2017 5:46	57	3/5/2017 6:51	55	4/5/2017 7:56	55	6/5/2017 1:01	56	7/5/2017 2:06	55		
1/5/2017 4:46	53	2/5/2017 5:51	53	3/5/2017 6:56	56	5/5/2017 0:01	56	6/5/2017 1:06	56	7/5/2017 2:11	55		
1/5/2017 4:51	52	2/5/2017 5:56	54	3/5/2017 7:01	57	5/5/2017 0:06	56	6/5/2017 1:11	56	7/5/2017 2:16	55		
1/5/2017 4:56	52	2/5/2017 6:01	55	3/5/2017 7:06	57	5/5/2017 0:11	56	6/5/2017 1:16	57	7/5/2017 2:21	55		
1/5/2017 5:01	53	2/5/2017 6:06	54	3/5/2017 7:11	57	5/5/2017 0:16	56	6/5/2017 1:21	57	7/5/2017 2:26	55		
1/5/2017 5:06	53	2/5/2017 6:11	56	3/5/2017 7:16	56	5/5/2017 0:21	55	6/5/2017 1:26	55	7/5/2017 2:31	55		
1/5/2017 5:11	53	2/5/2017 6:16	55	3/5/2017 7:21	56	5/5/2017 0:26	55	6/5/2017 1:31	55	7/5/2017 2:36	55		
1/5/2017 5:16	52	2/5/2017 6:21	55	3/5/2017 7:26	55	5/5/2017 0:31	55	6/5/2017 1:36	56	7/5/2017 2:41	55		
1/5/2017 5:21	53	2/5/2017 6:26	55	3/5/2017 7:31	56	5/5/2017 0:36	56	6/5/2017 1:41	55	7/5/2017 2:46	55		
1/5/2017 5:26	53	2/5/2017 6:31	57	3/5/2017 7:36	55	5/5/2017 0:41	55	6/5/2017 1:46	55	7/5/2017 2:51	55		
1/5/2017 5:31	52	2/5/2017 6:36	56	3/5/2017 7:41	55	5/5/2017 0:46	56	6/5/2017 1:51	56	7/5/2017 2:56	55		
1/5/2017 5:36	53	2/5/2017 6:41	56	3/5/2017 7:46	56	5/5/2017 0:51	55	6/5/2017 1:56	55	7/5/2017 3:01	56		
1/5/2017 5:41	52	2/5/2017 6:46	57	3/5/2017 7:51	56	5/5/2017 0:56	55	6/5/2017 2:01	55	7/5/2017 3:06	56		
1/5/2017 5:46	53	2/5/2017 6:51	56	3/5/2017 7:56	56	5/5/2017 1:01	55	6/5/2017 2:06	55	7/5/2017 3:11	55		
1/5/2017 5:51	54	2/5/2017 6:56	57	4/5/2017 0:01	56	5/5/2017 1:06	55	6/5/2017 2:11	55	7/5/2017 3:16	56		
1/5/2017 5:56	54	2/5/2017 7:01	40	4/5/2017 0:06	56	5/5/2017 1:11	56	6/5/2017					

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)													
7/5/2017 6:16	55	8/5/2017 23:21	58	10/5/2017 0:26	54	11/5/2017 1:31	53	12/5/2017 2:36	53	13/5/2017 3:41	54				
7/5/2017 6:21	55	8/5/2017 23:26	58	10/5/2017 0:31	54	11/5/2017 1:36	53	12/5/2017 2:41	53	13/5/2017 3:46	54				
7/5/2017 6:26	56	8/5/2017 23:31	58	10/5/2017 0:36	54	11/5/2017 1:41	53	12/5/2017 2:46	53	13/5/2017 3:51	54				
7/5/2017 6:31	55	8/5/2017 23:36	57	10/5/2017 0:41	54	11/5/2017 1:46	54	12/5/2017 2:51	52	13/5/2017 3:56	54				
7/5/2017 6:36	56	8/5/2017 23:41	57	10/5/2017 0:46	54	11/5/2017 1:51	53	12/5/2017 2:56	53	13/5/2017 4:01	55				
7/5/2017 6:41	55	8/5/2017 23:46	57	10/5/2017 0:51	54	11/5/2017 1:56	53	12/5/2017 3:01	54	13/5/2017 4:06	54				
7/5/2017 6:46	56	8/5/2017 23:51	56	10/5/2017 0:56	54	11/5/2017 2:01	53	12/5/2017 3:06	55	13/5/2017 4:11	54				
7/5/2017 6:51	56	8/5/2017 23:56	56	10/5/2017 1:01	54	11/5/2017 2:06	53	12/5/2017 3:11	53	13/5/2017 4:16	54				
7/5/2017 6:56	55	9/5/2017 0:01	57	10/5/2017 1:06	54	11/5/2017 2:11	53	12/5/2017 3:16	54	13/5/2017 4:21	55				
7/5/2017 23:01	56	9/5/2017 0:06	56	10/5/2017 1:11	54	11/5/2017 2:16	53	12/5/2017 3:21	53	13/5/2017 4:26	56				
7/5/2017 23:06	57	9/5/2017 0:11	56	10/5/2017 1:16	54	11/5/2017 2:21	53	12/5/2017 3:26	52	13/5/2017 4:31	54				
7/5/2017 23:11	56	9/5/2017 0:16	56	10/5/2017 1:21	54	11/5/2017 2:26	53	12/5/2017 3:31	53	13/5/2017 4:36	54				
7/5/2017 23:16	56	9/5/2017 0:21	56	10/5/2017 1:26	54	11/5/2017 2:31	53	12/5/2017 3:36	54	13/5/2017 4:41	55				
7/5/2017 23:21	56	9/5/2017 0:26	56	10/5/2017 1:31	54	11/5/2017 2:36	54	12/5/2017 3:41	53	13/5/2017 4:46	54				
7/5/2017 23:26	55	9/5/2017 0:31	55	10/5/2017 1:36	54	11/5/2017 2:41	52	12/5/2017 3:46	53	13/5/2017 4:51	55				
7/5/2017 23:31	55	9/5/2017 0:36	56	10/5/2017 1:41	54	11/5/2017 2:46	53	12/5/2017 3:51	54	13/5/2017 4:56	54				
7/5/2017 23:36	56	9/5/2017 0:41	55	10/5/2017 1:46	53	11/5/2017 2:51	52	12/5/2017 3:56	54	13/5/2017 5:01	54				
7/5/2017 23:41	56	9/5/2017 0:46	55	10/5/2017 1:51	54	11/5/2017 2:56	54	12/5/2017 4:01	55	13/5/2017 5:06	55				
7/5/2017 23:46	56	9/5/2017 0:51	55	10/5/2017 1:56	53	11/5/2017 3:01	56	12/5/2017 4:06	54	13/5/2017 5:11	55				
7/5/2017 23:51	56	9/5/2017 0:56	55	10/5/2017 2:01	54	11/5/2017 3:06	52	12/5/2017 4:11	54	13/5/2017 5:16	55				
7/5/2017 23:56	55	9/5/2017 1:01	55	10/5/2017 2:06	53	11/5/2017 3:11	52	12/5/2017 4:16	54	13/5/2017 5:21	55				
8/5/2017 0:01	55	9/5/2017 1:06	55	10/5/2017 2:11	53	11/5/2017 3:16	52	12/5/2017 4:21	54	13/5/2017 5:26	55				
8/5/2017 0:06	56	9/5/2017 1:11	55	10/5/2017 2:16	53	11/5/2017 3:21	53	12/5/2017 4:26	54	13/5/2017 5:31	55				
8/5/2017 0:11	55	9/5/2017 1:16	56	10/5/2017 2:21	53	11/5/2017 3:26	52	12/5/2017 4:31	54	13/5/2017 5:36	55				
8/5/2017 0:16	56	9/5/2017 1:21	57	10/5/2017 2:26	54	11/5/2017 3:31	52	12/5/2017 4:36	54	13/5/2017 5:41	55				
8/5/2017 0:21	55	9/5/2017 1:26	57	10/5/2017 2:31	54	11/5/2017 3:36	52	12/5/2017 4:41	54	13/5/2017 5:46	55				
8/5/2017 0:26	55	9/5/2017 1:31	56	10/5/2017 2:36	53	11/5/2017 3:41	53	12/5/2017 4:46	54	13/5/2017 5:51	55				
8/5/2017 0:31	55	9/5/2017 1:36	56	10/5/2017 2:41	53	11/5/2017 3:46	52	12/5/2017 4:51	55	13/5/2017 5:56	55				
8/5/2017 0:36	54	9/5/2017 1:41	56	10/5/2017 2:46	54	11/5/2017 3:51	52	12/5/2017 4:56	56	13/5/2017 6:01	55				
8/5/2017 0:41	54	9/5/2017 1:46	56	10/5/2017 2:51	53	11/5/2017 3:56	52	12/5/2017 5:01	56	13/5/2017 6:06	55				
8/5/2017 0:46	55	9/5/2017 1:51	56	10/5/2017 2:56	53	11/5/2017 4:01	52	12/5/2017 5:06	55	13/5/2017 6:11	56				
8/5/2017 0:51	54	9/5/2017 1:56	57	10/5/2017 3:01	53	11/5/2017 4:06	53	12/5/2017 5:11	55	13/5/2017 6:16	56				
8/5/2017 0:56	54	9/5/2017 2:01	57	10/5/2017 3:06	53	11/5/2017 4:11	52	12/5/2017 5:16	55	13/5/2017 6:21	56				
8/5/2017 1:01	55	9/5/2017 2:06	48	10/5/2017 3:11	53	11/5/2017 4:16	52	12/5/2017 5:21	55	13/5/2017 6:26	56				
8/5/2017 1:06	54	9/5/2017 2:11	47	10/5/2017 3:16	52	11/5/2017 4:21	52	12/5/2017 5:26	55	13/5/2017 6:31	56				
8/5/2017 1:11	55	9/5/2017 2:16	42	10/5/2017 3:21	51	11/5/2017 4:26	54	12/5/2017 5:31	56	13/5/2017 6:36	57				
8/5/2017 1:16	57	9/5/2017 2:21	58	10/5/2017 3:26	52	11/5/2017 4:31	54	12/5/2017 5:36	55	13/5/2017 6:41	57				
8/5/2017 1:21	54	9/5/2017 2:26	58	10/5/2017 3:31	53	11/5/2017 4:36	54	12/5/2017 5:41	56	13/5/2017 6:46	56				
8/5/2017 1:26	53	9/5/2017 2:31	58	10/5/2017 3:36	54	11/5/2017 4:41	54	12/5/2017 5:46	55	13/5/2017 6:51	57				
8/5/2017 1:31	55	9/5/2017 2:36	58	10/5/2017 3:41	54	11/5/2017 4:46	54	12/5/2017 5:51	56	13/5/2017 6:56	56				
8/5/2017 1:36	54	9/5/2017 2:41	58	10/5/2017 3:46	54	11/5/2017 4:51	54	12/5/2017 5:56	56	13/5/2017 23:01	57				
8/5/2017 1:41	54	9/5/2017 2:46	37	10/5/2017 3:51	55	11/5/2017 4:56	54	12/5/2017 6:01	55	13/5/2017 23:06	32				
8/5/2017 1:46	54	9/5/2017 2:51	42	10/5/2017 3:56	54	11/5/2017 5:01	54	12/5/2017 6:06	55	13/5/2017 23:11	56				
8/5/2017 1:51	55	9/5/2017 2:56	48	10/5/2017 4:01	54	11/5/2017 5:06	54	12/5/2017 6:11	55	13/5/2017 23:16	56				
8/5/2017 1:56	54	9/5/2017 3:01	58	10/5/2017 4:06	54	11/5/2017 5:11	54	12/5/2017 6:16	55	13/5/2017 23:21	57				
8/5/2017 2:01	54	9/5/2017 3:06	58	10/5/2017 4:11	54	11/5/2017 5:16	54	12/5/2017 6:21	55	13/5/2017 23:26	56				
8/5/2017 2:06	53	9/5/2017 3:11	58	10/5/2017 4:16	55	11/5/2017 5:21	53	12/5/2017 6:26	56	13/5/2017 23:31	56				
8/5/2017 2:11	54	9/5/2017 3:16	57	10/5/2017 4:21	55	11/5/2017 5:26	53	12/5/2017 6:31	57	13/5/2017 23:36	56				
8/5/2017 2:16	54	9/5/2017 3:21	57	10/5/2017 4:26	55	11/5/2017 5:31	53	12/5/2017 6:36	57	13/5/2017 23:41	56				
8/5/2017 2:21	55	9/5/2017 3:26	56	10/5/2017 4:31	57	11/5/2017 5:36	53	12/5/2017 6:41	56	13/5/2017 23:46	58				
8/5/2017 2:26	53	9/5/2017 3:31	56	10/5/2017 4:36	57	11/5/2017 5:41	54	12/5/2017 6:46	56	13/5/2017 23:51	56				
8/5/2017 2:31	53	9/5/2017 3:36	55	10/5/2017 4:41	55	11/5/2017 5:46	54	12/5/2017 6:51	56	13/5/2017 23:56	56				
8/5/2017 2:36	54	9/5/2017 3:41	55	10/5/2017 4:46	55	11/5/2017 5:51	53	12/5/2017 6:56	57	14/5/2017 0:01	56				
8/5/2017 2:41	53	9/5/2017 3:46	56	10/5/2017 4:51	55	11/5/2017 5:56	53	12/5/2017 23:01	57	14/5/2017 0:06	56				
8/5/2017 2:46	54	9/5/2017 3:51	55	10/5/2017 4:56	55	11/5/2017 6:01	54	12/5/2017 23:06	57	14/5/2017 0:11	56				
8/5/2017 2:51	54	9/5/2017 3:56	54	10/5/2017 5:01	55	11/5/2017 6:06	54	12/5/2017 23:11	58	14/5/2017 0:16	56				
8/5/2017 2:56	53	9/5/2017 4:01	54	10/5/2017 5:06	55	11/5/2017 6:11	54	12/5/2017 23:16	57	14/5/2017 0:21	56				
8/5/2017 3:01	53	9/5/2017 4:06	54	10/5/2017 5:11	55	11/5/2017 6:16	55	12/5/2017 23:21	57	14/5/2017 0:26	56				
8/5/2017 3:06	53	9/5/2017 4:11	53	10/5/2017 5:16	55	11/5/2017 6:21	55	12/5/2017 23:26	57	14/5/2017 0:31	57				
8/5/2017 3:11	54	9/5/2017 4:16	54	10/5/2017 5:21	55	11/5/2017 6:26	55	12/5/2017 23:31	58	14/5/2017 0:36	58				
8/5/2017 3:16	52	9/5/2017 4:21	54	10/5/2017 5:26	54	11/5/2017 6:31	55	12/5/2017 23:36	57	14/5/2017 0:41	56				
8/5/2017 3:21	53	9/5/2017 4:26	53	10/5/2017 5:31	54	11/5/2017 6:36	55	12/5/2017 23:41	57	14/5/2017 0:46	55				
8/5/2017 3:26	53	9/5/2017 4:31	53	10/5/2017 5:36	54	11/5/2017 6:41	57	12/5/2017 23:46	57	14/5/2017 0:51	56				
8/5/2017 3:31	48	9/5/2017 4:36	54	10/5/2017 5:41	55	11/5/2017 6:46	57	12/5/2017 23:51	57	14/5/2017 0:56	55				
8/5/2017 3:36	53	9/5/2017 4:41	55	10/5/2017 5:46	55	11/5/2017 6:51	57	12/5/2017 23:56	57	14/5/2017 1:01	56				
8/5/2017 3:41	53	9/5/2017 4:46	56	10/5/2017 5:51	55	11/5/2017 6:56	56	13/5/2017 0:01	57	14/5/2017 1:06	55				
8/5/2017 3:46	53	9/5/2017 4:51	55	10/5/2017 5:56	55	11/5/2017 23:01	55	13/5/2017 0:06	56	14/5/2017 1:11	56				
8/5/2017 3:51	53	9/5/2017 4:56	54	10/5/2017 6:01	56	11/5/2017 23:06	55	13/5/2017 0:11	56	14/5/2017 1:16	55				
8/5/2017 3:56	53	9/5/2017 5:01	54	10/5/2017 6:06	55	11/5/2017 23:11	55	13/5/2017 0:16	56	14/5/2017 1:21	56				
8/5/2017 4:01	53	9/5/2017													

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)													
14/5/2017 4:46	55	15/5/2017 5:51	54	16/5/2017 6:56	58	18/5/2017 0:01	57	19/5/2017 1:06	56	20/5/2017 2:11	54	21/5/2017 3:16	55	22/5/2017 4:21	55
14/5/2017 4:51	55	15/5/2017 5:56	54	16/5/2017 23:01	56	18/5/2017 0:06	56	19/5/2017 1:11	55	20/5/2017 2:16	55	21/5/2017 3:21	55	22/5/2017 4:26	55
14/5/2017 4:56	55	15/5/2017 6:01	55	16/5/2017 23:06	56	18/5/2017 0:11	56	19/5/2017 1:16	55	20/5/2017 2:21	54	21/5/2017 3:26	55	22/5/2017 4:31	55
14/5/2017 5:01	55	15/5/2017 6:06	56	16/5/2017 23:11	56	18/5/2017 0:16	55	19/5/2017 1:21	55	20/5/2017 2:26	55	21/5/2017 3:31	55	22/5/2017 4:36	55
14/5/2017 5:06	55	15/5/2017 6:11	55	16/5/2017 23:16	57	18/5/2017 0:21	55	19/5/2017 1:26	55	20/5/2017 2:31	54	21/5/2017 3:36	55	22/5/2017 4:41	55
14/5/2017 5:11	55	15/5/2017 6:16	55	16/5/2017 23:21	57	18/5/2017 0:26	55	19/5/2017 1:31	54	20/5/2017 2:36	54	21/5/2017 3:41	55	22/5/2017 4:46	55
14/5/2017 5:16	54	15/5/2017 6:21	55	16/5/2017 23:26	56	18/5/2017 0:31	55	19/5/2017 1:36	55	20/5/2017 2:41	54	21/5/2017 3:46	55	22/5/2017 4:51	55
14/5/2017 5:21	55	15/5/2017 6:26	55	16/5/2017 23:31	56	18/5/2017 0:36	55	19/5/2017 1:41	55	20/5/2017 2:46	53	21/5/2017 3:51	55	22/5/2017 4:56	55
14/5/2017 5:26	55	15/5/2017 6:31	56	16/5/2017 23:36	56	18/5/2017 0:41	54	19/5/2017 1:46	55	20/5/2017 2:51	54	21/5/2017 3:56	55	22/5/2017 5:01	55
14/5/2017 5:31	55	15/5/2017 6:36	56	16/5/2017 23:41	55	18/5/2017 0:46	54	19/5/2017 1:51	54	20/5/2017 3:01	54	21/5/2017 4:01	55	22/5/2017 5:06	55
14/5/2017 5:36	55	15/5/2017 6:41	56	16/5/2017 23:46	55	18/5/2017 0:51	55	19/5/2017 1:56	54	20/5/2017 3:06	54	21/5/2017 4:06	55	22/5/2017 5:11	55
14/5/2017 5:41	55	15/5/2017 6:46	57	16/5/2017 23:51	56	18/5/2017 0:56	54	19/5/2017 2:01	54	20/5/2017 3:11	54	21/5/2017 4:11	55	22/5/2017 5:16	54
14/5/2017 5:46	55	15/5/2017 6:51	56	16/5/2017 23:56	56	18/5/2017 1:01	57	19/5/2017 2:06	54	20/5/2017 3:16	53	21/5/2017 4:16	55	22/5/2017 5:21	54
14/5/2017 5:51	54	15/5/2017 6:56	56	17/5/2017 0:01	56	18/5/2017 1:06	54	19/5/2017 2:11	55	20/5/2017 3:21	55	21/5/2017 4:21	55	22/5/2017 5:26	54
14/5/2017 5:56	55	15/5/2017 23:01	56	17/5/2017 0:06	55	18/5/2017 1:11	54	19/5/2017 2:16	54	20/5/2017 3:26	54	21/5/2017 4:26	55	22/5/2017 5:31	54
14/5/2017 6:01	55	15/5/2017 23:06	56	17/5/2017 0:11	55	18/5/2017 1:16	54	19/5/2017 2:21	55	20/5/2017 3:31	53	21/5/2017 4:31	55	22/5/2017 5:36	53
14/5/2017 6:06	55	15/5/2017 23:11	56	17/5/2017 0:16	56	18/5/2017 1:21	54	19/5/2017 2:26	54	20/5/2017 3:36	53	21/5/2017 4:36	54	22/5/2017 5:41	54
14/5/2017 6:11	55	15/5/2017 23:16	56	17/5/2017 0:21	56	18/5/2017 1:26	54	19/5/2017 2:31	54	20/5/2017 3:41	53	21/5/2017 4:41	55	22/5/2017 5:46	54
14/5/2017 6:16	55	15/5/2017 23:21	51	17/5/2017 0:26	55	18/5/2017 1:31	54	19/5/2017 2:36	54	20/5/2017 3:46	53	21/5/2017 4:46	54		
14/5/2017 6:21	55	15/5/2017 23:26	57	17/5/2017 0:31	55	18/5/2017 1:36	55	19/5/2017 2:41	53	20/5/2017 3:51	53	21/5/2017 4:51	55		
14/5/2017 6:26	55	15/5/2017 23:31	56	17/5/2017 0:36	55	18/5/2017 1:41	55	19/5/2017 2:46	53	20/5/2017 3:56	52	21/5/2017 4:56	53		
14/5/2017 6:31	55	15/5/2017 23:36	56	17/5/2017 0:41	55	18/5/2017 1:46	55	19/5/2017 2:51	54	20/5/2017 4:01	54	21/5/2017 5:01	55		
14/5/2017 6:36	55	15/5/2017 23:41	56	17/5/2017 0:46	55	18/5/2017 1:51	55	19/5/2017 2:56	54	20/5/2017 4:06	54	21/5/2017 5:06	54		
14/5/2017 6:41	58	15/5/2017 23:46	56	17/5/2017 0:51	55	18/5/2017 1:56	55	19/5/2017 3:01	54	20/5/2017 4:11	53	21/5/2017 5:11	55		
14/5/2017 6:46	56	15/5/2017 23:51	56	17/5/2017 0:56	54	18/5/2017 2:01	54	19/5/2017 3:06	54	20/5/2017 4:16	52	21/5/2017 5:16	54		
14/5/2017 6:51	55	15/5/2017 23:56	55	17/5/2017 1:01	54	18/5/2017 2:06	53	19/5/2017 3:11	53	20/5/2017 4:21	54	21/5/2017 5:21	54		
14/5/2017 6:56	55	16/5/2017 0:01	55	17/5/2017 1:06	54	18/5/2017 2:11	53	19/5/2017 3:16	56	20/5/2017 4:26	55	21/5/2017 5:26	54		
14/5/2017 23:01	56	16/5/2017 0:06	55	17/5/2017 1:11	54	18/5/2017 2:16	53	19/5/2017 3:21	55	20/5/2017 4:31	54	21/5/2017 5:31	54		
14/5/2017 23:06	56	16/5/2017 0:11	55	17/5/2017 1:16	55	18/5/2017 2:21	53	19/5/2017 3:26	53	20/5/2017 4:36	54	21/5/2017 5:36	53		
14/5/2017 23:11	57	16/5/2017 0:16	55	17/5/2017 1:21	55	18/5/2017 2:26	54	19/5/2017 3:31	53	20/5/2017 4:41	54	21/5/2017 5:41	54		
14/5/2017 23:16	57	16/5/2017 0:21	55	17/5/2017 1:26	57	18/5/2017 2:31	53	19/5/2017 3:36	53	20/5/2017 4:46	53	21/5/2017 5:46	55		
14/5/2017 23:21	56	16/5/2017 0:26	56	17/5/2017 1:31	56	18/5/2017 2:36	53	19/5/2017 3:41	53	20/5/2017 4:51	55	21/5/2017 5:51	55		
14/5/2017 23:26	56	16/5/2017 0:31	55	17/5/2017 1:36	56	18/5/2017 2:41	53	19/5/2017 3:46	53	20/5/2017 4:56	53	21/5/2017 5:56	54		
14/5/2017 23:31	57	16/5/2017 0:36	55	17/5/2017 1:41	55	18/5/2017 2:46	53	19/5/2017 3:51	53	20/5/2017 5:01	53	21/5/2017 6:01	54		
14/5/2017 23:36	56	16/5/2017 0:41	56	17/5/2017 1:46	54	18/5/2017 2:51	53	19/5/2017 3:56	52	20/5/2017 5:06	53	21/5/2017 6:06	54		
14/5/2017 23:41	56	16/5/2017 0:46	56	17/5/2017 1:51	55	18/5/2017 2:56	56	19/5/2017 4:01	54	20/5/2017 5:11	52	21/5/2017 6:11	54		
14/5/2017 23:46	56	16/5/2017 0:51	58	17/5/2017 1:56	56	18/5/2017 3:01	53	19/5/2017 4:06	54	20/5/2017 5:16	53	21/5/2017 6:16	55		
14/5/2017 23:51	56	16/5/2017 0:56	56	17/5/2017 2:01	54	18/5/2017 3:06	53	19/5/2017 4:11	53	20/5/2017 5:21	54	21/5/2017 6:21	55		
14/5/2017 23:56	56	16/5/2017 1:01	58	17/5/2017 2:06	54	18/5/2017 3:11	53	19/5/2017 4:16	52	20/5/2017 5:26	53	21/5/2017 6:26	55		
15/5/2017 0:01	55	16/5/2017 1:06	57	17/5/2017 2:11	54	18/5/2017 3:16	53	19/5/2017 4:21	54	20/5/2017 5:31	53	21/5/2017 6:31	55		
15/5/2017 0:06	55	16/5/2017 1:11	58	17/5/2017 2:16	54	18/5/2017 3:21	53	19/5/2017 4:26	54	20/5/2017 5:36	54	21/5/2017 6:36	56		
15/5/2017 0:11	55	16/5/2017 1:16	57	17/5/2017 2:21	54	18/5/2017 3:26	53	19/5/2017 4:31	54	20/5/2017 5:41	54	21/5/2017 6:41	55		
15/5/2017 0:16	55	16/5/2017 1:21	56	17/5/2017 2:26	53	18/5/2017 3:31	54	19/5/2017 4:36	55	20/5/2017 5:46	55	21/5/2017 6:46	56		
15/5/2017 0:21	55	16/5/2017 1:26	52	17/5/2017 2:31	53	18/5/2017 3:36	54	19/5/2017 4:41	54	20/5/2017 5:51	54	21/5/2017 6:51	56		
15/5/2017 0:26	55	16/5/2017 1:31	54	17/5/2017 2:36	53	18/5/2017 3:41	54	19/5/2017 4:46	55	20/5/2017 5:56	54	21/5/2017 6:56	55		
15/5/2017 0:31	54	16/5/2017 1:36	58	17/5/2017 2:41	53	18/5/2017 3:46	54	19/5/2017 4:51	54	20/5/2017 6:01	54	21/5/2017 7:01	55		
15/5/2017 0:36	55	16/5/2017 1:41	56	17/5/2017 2:46	54	18/5/2017 3:51	53	19/5/2017 4:56	53	20/5/2017 6:06	54	21/5/2017 7:06	56		
15/5/2017 0:41	54	16/5/2017 1:46	56	17/5/2017 2:51	56	18/5/2017 3:56	53	19/5/2017 5:01	53	20/5/2017 6:11	55	21/5/2017 7:11	55		
15/5/2017 0:46	56	16/5/2017 1:51	55	17/5/2017 2:56	53	18/5/2017 4:01	54	19/5/2017 5:06	53	20/5/2017 6:16	55	21/5/2017 7:16	55		
15/5/2017 0:51	55	16/5/2017 1:56	55	17/5/2017 3:01	54	18/5/2017 4:06	54	19/5/2017 5:11	52	20/5/2017 6:21	55	21/5/2017 7:21	55		
15/5/2017 0:56	56	16/5/2017 2:01	55	17/5/2017 3:06	53	18/5/2017 4:11	53	19/5/2017 5:16	53	20/5/2017 6:26	57	21/5/2017 7:26	56		
15/5/2017 1:01	55	16/5/2017 2:06	55	17/5/2017 3:11	53	18/5/2017 4:16	53	19/5/2017 5:21	54	20/5/2017 6:31	58	21/5/2017 7:31	56		
15/5/2017 1:06	55	16/5/2017 2:11	55	17/5/2017 3:16	53	18/5/2017 4:21	54	19/5/2017 5:26	53	20/5/2017 6:36	57	21/5/2017 7:36	57		
15/5/2017 1:11	56	16/5/2017 2:16	55	17/5/2017 3:21	53	18/5/2017 4:26	54	19/5/2017 5:31	53	20/5/2017 6:41	56	21/5/2017 7:41	55		
15/5/2017 1:16	55	16/5/2017 2:21	55	17/5/2017 3:26	53	18/5/2017 4:31	53	19/5/2017 5:36	54	20/5/2017 6:46	55	21/5/2017 7:46	56		
15/5/2017 1:21	57	16/5/2017 2:26	54	17/5/2017 3:31	54	18/5/2017 4:36	55	19/5/2017 5:41	54	20/5/2017 6:51	54	21/5/2017 7:51	55		
15/5/2017 1:26	55	16/5/2017 2:31	54	17/5/2017 3:36	53	18/5/2017 4:41	55	19/5/2017 5:46	53	20/5/2017 6:56	56	21/5/2017 7:56	56		
15/5/2017 1:31	55	16/5/2017 2:36	54	17/5/2017 3:41	53	18/5/2017 4:46	55	19/5/2017 5:51	54	20/5/2017 7:01	55	21/5/2017 8:01	55		
15/5/2017 1:36	55	16/5/2017 2:41	54	17/5/2017 3:46	53	18/5/2017 4:51	55	19/5/2017 5:56	54	20/5/2017 7:06	54	21/5/2017 8:06	55		
15/5/2017 1:41	55	16/5/2017 2:46	54	17/5/2017 3:51	53	18/5/2017 4:56	57	19/5/2017 6:01	54	20/5/2017 7:11	55	21/5/2017 8:11	55		
15/5/2017 1:46	55	16/5/2017 2:51	54	17/5/2017 3:56	54	18/5/2017 5:01	54	19/5/2017 6:06	54	20/5/2017 7:16	55	21/5/2017 8:16	55		
15/5/2017 1:51	55	16/5/2017 2:56	54	17/5/2017 4:01	54	18/5/2017 5:06	55	19/5/							

Real-time Noise Data RTN2a (Hong Kong Electric Centre)

21/5/2017 3:16	54	22/5/2017 4:21	53	23/5/2017 5:26	56
21/5/2017 3:21	54	22/5/2017 4:26	53	23/5/2017 5:31	54
21/5/2017 3:26	54	22/5/2017 4:31	53	23/5/2017 5:36	55
21/5/2017 3:31	54	22/5/2017 4:36	53	23/5/2017 5:41	55
21/5/2017 3:36	54	22/5/2017 4:41	53	23/5/2017 5:46	55
21/5/2017 3:41	53	22/5/2017 4:46	53	23/5/2017 5:51	55
21/5/2017 3:46	54	22/5/2017 4:51	53	23/5/2017 5:56	55
21/5/2017 3:51	53	22/5/2017 4:56	53	23/5/2017 6:01	55
21/5/2017 3:56	53	22/5/2017 5:01	53	23/5/2017 6:06	55
21/5/2017 4:01	54	22/5/2017 5:06	53	23/5/2017 6:11	55
21/5/2017 4:06	54	22/5/2017 5:11	53	23/5/2017 6:16	56
21/5/2017 4:11	54	22/5/2017 5:16	54	23/5/2017 6:21	56
21/5/2017 4:16	54	22/5/2017 5:21	54	23/5/2017 6:26	56
21/5/2017 4:21	56	22/5/2017 5:26	53	23/5/2017 6:31	56
21/5/2017 4:26	54	22/5/2017 5:31	54	23/5/2017 6:36	56
21/5/2017 4:31	54	22/5/2017 5:36	54	23/5/2017 6:41	57
21/5/2017 4:36	54	22/5/2017 5:41	54	23/5/2017 6:46	58
21/5/2017 4:41	53	22/5/2017 5:46	54	23/5/2017 6:51	57
21/5/2017 4:46	55	22/5/2017 5:51	54	23/5/2017 6:56	42
21/5/2017 4:51	53	22/5/2017 5:56	54	23/5/2017 23:01	57
21/5/2017 4:56	53	22/5/2017 6:01	55	23/5/2017 23:06	56
21/5/2017 5:01	54	22/5/2017 6:06	54	23/5/2017 23:11	57
21/5/2017 5:06	54	22/5/2017 6:11	55	23/5/2017 23:16	58
21/5/2017 5:11	53	22/5/2017 6:16	55	23/5/2017 23:21	56
21/5/2017 5:16	53	22/5/2017 6:21	56	23/5/2017 23:26	55
21/5/2017 5:21	54	22/5/2017 6:26	55	23/5/2017 23:31	56
21/5/2017 5:26	54	22/5/2017 6:31	56	23/5/2017 23:36	56
21/5/2017 5:31	55	22/5/2017 6:36	55	23/5/2017 23:41	56
21/5/2017 5:36	54	22/5/2017 6:41	56	23/5/2017 23:46	56
21/5/2017 5:41	55	22/5/2017 6:46	56	23/5/2017 23:51	56
21/5/2017 5:46	55	22/5/2017 6:51	56	23/5/2017 23:56	57
21/5/2017 5:51	55	22/5/2017 6:56	56	24/5/2017 0:01	57
21/5/2017 5:56	53	22/5/2017 23:01	58	24/5/2017 0:06	56
21/5/2017 6:01	53	22/5/2017 23:06	47	24/5/2017 0:11	56
21/5/2017 6:06	55	22/5/2017 23:11	45	24/5/2017 0:16	56
21/5/2017 6:11	54	22/5/2017 23:16	58	24/5/2017 0:21	57
21/5/2017 6:16	55	22/5/2017 23:21	57	24/5/2017 0:26	56
21/5/2017 6:21	55	22/5/2017 23:26	57	24/5/2017 0:31	55
21/5/2017 6:26	55	22/5/2017 23:31	57	24/5/2017 0:36	56
21/5/2017 6:31	55	22/5/2017 23:36	56	24/5/2017 0:41	56
21/5/2017 6:36	55	22/5/2017 23:41	56	24/5/2017 0:46	56
21/5/2017 6:41	55	22/5/2017 23:46	56	24/5/2017 0:51	55
21/5/2017 6:46	56	22/5/2017 23:51	56	24/5/2017 0:56	57
21/5/2017 6:51	56	22/5/2017 23:56	56	24/5/2017 1:01	55
21/5/2017 6:56	56	23/5/2017 0:01	56	24/5/2017 1:06	55
21/5/2017 23:01	55	23/5/2017 0:06	55	24/5/2017 1:11	56
21/5/2017 23:06	56	23/5/2017 0:11	56	24/5/2017 1:16	55
21/5/2017 23:11	55	23/5/2017 0:16	57	24/5/2017 1:21	55
21/5/2017 23:16	56	23/5/2017 0:21	57	24/5/2017 1:26	55
21/5/2017 23:21	55	23/5/2017 0:26	57	24/5/2017 1:31	55
21/5/2017 23:26	55	23/5/2017 0:31	56	24/5/2017 1:36	56
21/5/2017 23:31	56	23/5/2017 0:36	56	24/5/2017 1:41	56
21/5/2017 23:36	55	23/5/2017 0:41	57	24/5/2017 1:46	54
21/5/2017 23:41	55	23/5/2017 0:46	56	24/5/2017 1:51	54
21/5/2017 23:46	55	23/5/2017 0:51	55	24/5/2017 1:56	53
21/5/2017 23:51	56	23/5/2017 0:56	55	24/5/2017 2:01	53
21/5/2017 23:56	56	23/5/2017 1:01	55	24/5/2017 2:06	53
22/5/2017 0:01	55	23/5/2017 1:06	55	24/5/2017 2:11	53
22/5/2017 0:06	55	23/5/2017 1:11	55	24/5/2017 2:16	53
22/5/2017 0:11	55	23/5/2017 1:16	55	24/5/2017 2:21	53
22/5/2017 0:16	55	23/5/2017 1:21	55	24/5/2017 2:26	53
22/5/2017 0:21	55	23/5/2017 1:26	54	24/5/2017 2:31	53
22/5/2017 0:26	55	23/5/2017 1:31	54	24/5/2017 2:36	54
22/5/2017 0:31	55	23/5/2017 1:36	55	24/5/2017 2:41	54
22/5/2017 0:36	55	23/5/2017 1:41	55	24/5/2017 2:46	53
22/5/2017 0:41	54	23/5/2017 1:46	55	24/5/2017 2:51	53
22/5/2017 0:46	54	23/5/2017 1:51	55	24/5/2017 2:56	53
22/5/2017 0:51	54	23/5/2017 1:56	54	24/5/2017 3:01	52
22/5/2017 0:56	54	23/5/2017 2:01	55	24/5/2017 3:06	53
22/5/2017 1:01	56	23/5/2017 2:06	55	24/5/2017 3:11	53
22/5/2017 1:06	57	23/5/2017 2:11	55	24/5/2017 3:16	54
22/5/2017 1:11	54	23/5/2017 2:16	55	24/5/2017 3:21	53
22/5/2017 1:16	54	23/5/2017 2:21	55	24/5/2017 3:26	54
22/5/2017 1:21	54	23/5/2017 2:26	55	24/5/2017 3:31	55
22/5/2017 1:26	54	23/5/2017 2:31	55	24/5/2017 3:36	55
22/5/2017 1:31	53	23/5/2017 2:36	54	24/5/2017 3:41	54
22/5/2017 1:36	54	23/5/2017 2:41	54	24/5/2017 3:46	54
22/5/2017 1:41	53	23/5/2017 2:46	55	24/5/2017 3:51	54
22/5/2017 1:46	53	23/5/2017 2:51	55	24/5/2017 3:56	54
22/5/2017 1:51	53	23/5/2017 2:56	54	24/5/2017 4:01	55
22/5/2017 1:56	53	23/5/2017 3:01	54	24/5/2017 4:06	55
22/5/2017 2:01	54	23/5/2017 3:06	54	24/5/2017 4:11	55
22/5/2017 2:06	53	23/5/2017 3:11	54	24/5/2017 4:16	54
22/5/2017 2:11	53	23/5/2017 3:16	54	24/5/2017 4:21	54
22/5/2017 2:16	53	23/5/2017 3:21	54	24/5/2017 4:26	53
22/5/2017 2:21	53	23/5/2017 3:26	55	24/5/2017 4:31	54
22/5/2017 2:26	53	23/5/2017 3:31	54	24/5/2017 4:36	53
22/5/2017 2:31	53	23/5/2017 3:36	54	24/5/2017 4:41	54
22/5/2017 2:36	53	23/5/2017 3:41	54	24/5/2017 4:46	53
22/5/2017 2:41	52	23/5/2017 3:46	55	24/5/2017 4:51	53
22/5/2017 2:46	53	23/5/2017 3:51	54	24/5/2017 4:56	53
22/5/2017 2:51	53	23/5/2017 3:56	55	24/5/2017 5:01	54
22/5/2017 2:56	52	23/5/2017 4:01	54	24/5/2017 5:06	54
22/5/2017 3:01	53	23/5/2017 4:06	54	24/5/2017 5:11	54
22/5/2017 3:06	52	23/5/2017 4:11	54	24/5/2017 5:16	54
22/5/2017 3:11	53	23/5/2017 4:16	55	24/5/2017 5:21	54
22/5/2017 3:16	53	23/5/2017 4:21	54	24/5/2017 5:26	54
22/5/2017 3:21	53	23/5/2017 4:26	55	24/5/2017 5:31	54
22/5/2017 3:26	53	23/5/2017 4:31	55	24/5/2017 5:36	54
22/5/2017 3:31	53	23/5/2017 4:36	55	24/5/2017 5:41	54
22/5/2017 3:36	53	23/5/2017 4:41	54	24/5/2017 5:46	54
22/5/2017 3:41	53	23/5/2017 4:46	54	24/5/2017 5:51	54
22/5/2017 3:46	53	23/5/2017 4:51	56	24/5/2017 5:56	56
22/5/2017 3:51	53	23/5/2017 4:56	55	24/5/2017 6:01	63
22/5/2017 3:56	53	23/5/2017 5:01	54	24/5/2017 6:06	59
22/5/2017 4:01	53	23/5/2017 5:06	54	24/5/2017 6:11	61
22/5/2017 4:06	53	23/5/2017 5:11	54	24/5/2017 6:16	60
22/5/2017 4:11	53	23/5/2017 5:16	54	24/5/2017 6:21	61
22/5/2017 4:16	53	23/5/2017 5:21	54	24/5/2017 6:26	61

24/5/2017 6:31	68
24/5/2017 6:36	66
24/5/2017 6:41	61
24/5/2017 6:46	59
24/5/2017 6:51	57
24/5/2017 6:56	70
24/5/2017 23:01	56
24/5/2017 23:06	56
24/5/2017 23:11	56
24/5/2017 23:16	58
24/5/2017 23:21	58
24/5/2017 23:26	56
24/5/2017 23:31	58
24/5/2017 23:36	56
24/5/2017 23:41	56
24/5/2017 23:46	56
24/5/2017 23:51	56
24/5/2017 23:56	56
25/5/2017 0:01	55
25/5/2017 0:06	56
25/5/2017 0:11	56
25/5/2017 0:16	56
25/5/2017 0:21	57
25/5/2017 0:26	57
25/5/2017 0:31	55
25/5/2017 0:36	55
25/5/2017 0:41	56
25/5/2017 0:46	56
25/5/2017 0:51	56
25/5/2017 0:56	55
25/5/2017 1:01	55
25/5/2017 1:06	55
25/5/2017 1:11	55
25/5/2017 1:16	55
25/5/2017 1:21	55
25/5/2017 1:26	55
25/5/2017 1:31	54
25/5/2017 1:36	55
25/5/2017 1:41	55
25/5/2017 1:46	54
25/5/2017 1:51	55
25/5/2017 1:56	55
25/5/2017 2:01	55
25/5/2017 2:06	55
25/5/2017 2:11	54
25/5/2017 2:16	54
25/5/2017 2:21	54
25/5/2017 2:26	54
25/5/2017 2:31	54
25/5/2017 2:36	54
25/5/2017 2:41	54
25/5/2017 2:46	56
25/5/2017 2:51	53
25/5/2017 2:56	54
25/5/2017 3:01	54
25/5/2017 3:06	54
25/5/2017 3:11	53
25/5/2017 3:16	53
25/5/2017 3:21	53
25/5/2017 3:26	53
25/5/2017 3:31	53
25/5/2017 3:36	54
25/5/2017 3:41	53
25/5/2017 3:46	53
25/5/2017 3:51	53
25/5/2017 3:56	53
25/5/2017 4:01	54
25/5/2017 4:06	54
25/5/2017 4:11	54
25/5/2017 4:16	54
25/5/2017 4:21	54
25/5/2017 4:26	53
25/5/2017 4:31	53
25/5/2017 4:36	53
25/5/2017 4:41	54
25/5/2017 4:46	53
25/5/2017 4:51	54
25/5/2017 4:56	53
25/5/2017 5:01	54
25/5/2017 5:06	54
25/5/2017 5:11	54
25/5/2017 5:16	54
25/5/2017 5:21	54
25/5/2017 5:26	54
25/5/2017 5:31	54
25/5/2017 5:36	54
25/5/2017 5:41	54
25/5/2017 5:46	55
25/5/2017 5:51	54
25/5/2017 5:56	56
25/5/2017 6:01	55
25/5/2017 6:06	55
25/5/2017 6:11	55
25/5/2017 6:16	56
25/5/2017 6:21	56
25/5/2017 6:26	56
25/5/2017 6:31	56
25/5/2017 6:36	57
25/5/2017 6:41	57
25/5/2017 6:46	57
25/5/2017 6:51	57
25/5/2017 6:56	58
25/5/2017 23:01	56
25/5/2017 23:06	56
25/5/2017 23:11	58
25/5/2017 23:16	56
25/5/2017 23:21	57
25/5/2017 23:26	56
25/5/2017 23:31	56

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
Normal Day 07:00-19:00		4/5/2017 13:01	68	10/5/2017 7:31	76	15/5/2017 14:01	68	20/5/2017 8:31	67	25/5/2017 15:01	65
27/4/2017 7:01	66	4/5/2017 13:31	68	10/5/2017 8:01	65	15/5/2017 14:31	66	20/5/2017 9:01	67	25/5/2017 15:31	64
27/4/2017 7:31	66	4/5/2017 14:01	67	10/5/2017 8:31	66	15/5/2017 15:01	68	20/5/2017 9:31	67	25/5/2017 16:01	66
27/4/2017 8:01	65	4/5/2017 14:31	66	10/5/2017 9:01	68	15/5/2017 15:31	68	20/5/2017 10:01	66	25/5/2017 16:31	67
27/4/2017 8:31	64	4/5/2017 15:01	65	10/5/2017 9:31	68	15/5/2017 16:01	67	20/5/2017 10:31	67	25/5/2017 17:01	66
27/4/2017 9:01	64	4/5/2017 15:31	65	10/5/2017 10:01	66	15/5/2017 16:31	67	20/5/2017 11:01	67	25/5/2017 17:31	67
27/4/2017 9:31	66	4/5/2017 16:01	66	10/5/2017 10:31	67	15/5/2017 17:01	66	20/5/2017 11:31	67	25/5/2017 18:01	67
27/4/2017 10:01	67	4/5/2017 16:31	67	10/5/2017 11:01	68	15/5/2017 17:31	66	20/5/2017 12:01	67	25/5/2017 18:31	67
27/4/2017 10:31	67	4/5/2017 17:01	67	10/5/2017 11:31	67	15/5/2017 18:01	66	20/5/2017 12:31	65	26/5/2017 7:01	66
27/4/2017 11:01	67	4/5/2017 17:31	67	10/5/2017 12:01	67	15/5/2017 18:31	66	20/5/2017 13:01	65	26/5/2017 7:31	65
27/4/2017 11:31	67	4/5/2017 18:01	66	10/5/2017 12:31	68	16/5/2017 7:01	66	20/5/2017 13:31	66	26/5/2017 8:01	64
27/4/2017 12:01	65	4/5/2017 18:31	66	10/5/2017 13:01	67	16/5/2017 7:31	65	20/5/2017 14:01	65	26/5/2017 8:31	65
27/4/2017 12:31	66	5/5/2017 7:01	67	10/5/2017 13:31	67	16/5/2017 8:01	66	20/5/2017 14:31	67	26/5/2017 9:01	65
27/4/2017 13:01	67	5/5/2017 7:31	67	10/5/2017 14:01	67	16/5/2017 8:31	67	20/5/2017 15:01	67	26/5/2017 9:31	65
27/4/2017 13:31	68	5/5/2017 8:01	67	10/5/2017 14:31	67	16/5/2017 9:01	68	20/5/2017 15:31	67	26/5/2017 10:01	66
27/4/2017 14:01	68	5/5/2017 8:31	67	10/5/2017 15:01	67	16/5/2017 9:31	67	20/5/2017 16:01	67	26/5/2017 10:31	66
27/4/2017 14:31	68	5/5/2017 9:01	67	10/5/2017 15:31	67	16/5/2017 10:01	69	20/5/2017 16:31	67	26/5/2017 11:01	66
27/4/2017 15:01	67	5/5/2017 9:31	68	10/5/2017 16:01	67	16/5/2017 10:31	67	20/5/2017 17:01	66	26/5/2017 11:31	65
27/4/2017 15:31	67	5/5/2017 10:01	67	10/5/2017 16:31	68	16/5/2017 11:01	67	20/5/2017 17:31	66	26/5/2017 12:01	67
27/4/2017 16:01	68	5/5/2017 10:31	68	10/5/2017 17:01	67	16/5/2017 11:31	67	20/5/2017 18:01	66	26/5/2017 12:31	67
27/4/2017 16:31	67	5/5/2017 11:01	67	10/5/2017 17:31	67	16/5/2017 12:01	66	20/5/2017 18:31	66	26/5/2017 13:01	66
27/4/2017 17:01	67	5/5/2017 11:31	67	10/5/2017 18:01	67	16/5/2017 12:31	67	22/5/2017 7:01	65	26/5/2017 13:31	67
27/4/2017 17:31	66	5/5/2017 12:01	66	10/5/2017 18:31	66	16/5/2017 13:01	68	22/5/2017 7:31	64	26/5/2017 14:01	67
27/4/2017 18:01	67	5/5/2017 12:31	67	11/5/2017 7:01	67	16/5/2017 13:31	67	22/5/2017 8:01	65	26/5/2017 14:31	67
27/4/2017 18:31	67	5/5/2017 13:01	67	11/5/2017 7:31	66	16/5/2017 14:01	67	22/5/2017 8:31	65	26/5/2017 15:01	67
28/4/2017 7:01	66	5/5/2017 13:31	67	11/5/2017 8:01	66	16/5/2017 14:31	65	22/5/2017 9:01	65	26/5/2017 15:31	66
28/4/2017 7:31	67	5/5/2017 14:01	67	11/5/2017 8:31	65	16/5/2017 15:01	67	22/5/2017 9:31	65	26/5/2017 16:01	66
28/4/2017 8:01	66	5/5/2017 14:31	68	11/5/2017 9:01	66	16/5/2017 15:31	68	22/5/2017 10:01	65	26/5/2017 16:31	67
28/4/2017 8:31	66	5/5/2017 15:01	66	11/5/2017 9:31	67	16/5/2017 16:01	67	22/5/2017 10:31	67	26/5/2017 17:01	66
28/4/2017 9:01	67	5/5/2017 15:31	67	11/5/2017 10:01	68	16/5/2017 16:31	68	22/5/2017 11:01	67	26/5/2017 17:31	66
28/4/2017 9:31	67	5/5/2017 16:01	67	11/5/2017 10:31	68	16/5/2017 17:01	67	22/5/2017 11:31	67	26/5/2017 18:01	66
28/4/2017 10:01	66	5/5/2017 16:31	67	11/5/2017 11:01	67	16/5/2017 17:31	67	22/5/2017 12:01	67	<u>Normal Day 19:00-23:00</u> <u>Sunday & Holiday</u> <u>07:00-23:00</u>	
28/4/2017 10:31	67	5/5/2017 17:01	67	11/5/2017 11:31	66	16/5/2017 18:01	68	22/5/2017 12:31	66		
28/4/2017 11:01	67	5/5/2017 17:31	67	11/5/2017 12:01	65	16/5/2017 18:31	66	22/5/2017 13:01	64		
28/4/2017 11:31	67	5/5/2017 18:01	66	11/5/2017 12:31	67	17/5/2017 7:01	66	22/5/2017 13:31	67		
28/4/2017 12:01	67	5/5/2017 18:31	66	11/5/2017 13:01	67	17/5/2017 7:31	65	22/5/2017 14:01	67		
28/4/2017 12:31	68	6/5/2017 7:01	66	11/5/2017 13:31	67	17/5/2017 8:01	68	22/5/2017 14:31	67	27/4/2017 19:01	66
28/4/2017 13:01	68	6/5/2017 7:31	67	11/5/2017 14:01	65	17/5/2017 8:31	65	22/5/2017 15:01	67	27/4/2017 19:06	66
28/4/2017 13:31	68	6/5/2017 8:01	67	11/5/2017 14:31	66	17/5/2017 9:01	67	22/5/2017 15:31	67	27/4/2017 19:11	66
28/4/2017 14:01	66	6/5/2017 8:31	67	11/5/2017 15:01	67	17/5/2017 9:31	66	22/5/2017 16:01	63	27/4/2017 19:16	66
28/4/2017 14:31	67	6/5/2017 9:01	67	11/5/2017 15:31	66	17/5/2017 10:01	65	22/5/2017 16:31	67	27/4/2017 19:21	66
28/4/2017 15:01	66	6/5/2017 9:31	67	11/5/2017 16:01	70	17/5/2017 10:31	66	22/5/2017 17:01	67	27/4/2017 19:26	66
28/4/2017 15:31	66	6/5/2017 10:01	67	11/5/2017 16:31	69	17/5/2017 11:01	67	22/5/2017 17:31	66	27/4/2017 19:26	66
28/4/2017 16:01	67	6/5/2017 10:31	66	11/5/2017 17:01	68	17/5/2017 11:31	67	22/5/2017 18:01	66	27/4/2017 19:31	66
28/4/2017 16:31	67	6/5/2017 11:01	67	11/5/2017 17:31	68	17/5/2017 12:01	66	22/5/2017 18:31	66	27/4/2017 19:36	66
28/4/2017 17:01	67	6/5/2017 11:31	67	11/5/2017 18:01	67	17/5/2017 12:31	67	23/5/2017 7:01	67	27/4/2017 19:41	66
28/4/2017 17:31	66	6/5/2017 12:01	67	11/5/2017 18:31	65	17/5/2017 13:01	68	23/5/2017 7:31	66	27/4/2017 19:46	66
28/4/2017 18:01	67	6/5/2017 12:31	66	12/5/2017 7:01	66	17/5/2017 13:31	68	23/5/2017 8:01	66	27/4/2017 19:51	50
28/4/2017 18:31	66	6/5/2017 13:01	66	12/5/2017 7:31	66	17/5/2017 14:01	68	23/5/2017 8:31	65	27/4/2017 19:56	66
29/4/2017 7:01	66	6/5/2017 13:31	67	12/5/2017 8:01	66	17/5/2017 14:31	65	23/5/2017 9:01	66	27/4/2017 20:01	66
29/4/2017 7:31	66	6/5/2017 14:01	67	12/5/2017 8:31	68	17/5/2017 15:01	64	23/5/2017 9:31	68	27/4/2017 20:06	67
29/4/2017 8:01	67	6/5/2017 14:31	66	12/5/2017 9:01	66	17/5/2017 15:31	65	23/5/2017 10:01	68	27/4/2017 20:11	54
29/4/2017 8:31	68	6/5/2017 15:01	67	12/5/2017 9:31	67	17/5/2017 16:01	68	23/5/2017 10:31	67	27/4/2017 20:16	66
29/4/2017 9:01	67	6/5/2017 15:31	67	12/5/2017 10:01	67	17/5/2017 16:31	67	23/5/2017 11:01	67	27/4/2017 20:21	66
29/4/2017 9:31	67	6/5/2017 16:01	67	12/5/2017 10:31	67	17/5/2017 17:01	67	23/5/2017 11:31	67	27/4/2017 20:26	66
29/4/2017 10:01	65	6/5/2017 16:31	67	12/5/2017 11:01	68	17/5/2017 17:31	67	23/5/2017 12:01	67	27/4/2017 20:31	66
29/4/2017 10:31	66	6/5/2017 17:01	67	12/5/2017 11:31	64	17/5/2017 18:01	67	23/5/2017 12:31	65	27/4/2017 20:36	66
29/4/2017 11:01	65	6/5/2017 17:31	66	12/5/2017 12:01	64	17/5/2017 18:31	66	23/5/2017 13:01	66	27/4/2017 20:41	65
29/4/2017 11:31	67	6/5/2017 18:01	67	12/5/2017 12:31	66	18/5/2017 7:01					

Real-time Noise Data	RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)				
28/4/2017 21:01 66	30/4/2017 10:06 66	30/4/2017 19:11 66	1/5/2017 12:16 66	1/5/2017 21:21 64	3/5/2017 10:26 66
28/4/2017 21:06 66	30/4/2017 10:11 65	30/4/2017 19:16 65	1/5/2017 12:21 66	1/5/2017 21:26 65	3/5/2017 10:31 66
28/4/2017 21:11 66	30/4/2017 10:16 54	30/4/2017 19:21 66	1/5/2017 12:26 66	1/5/2017 21:31 64	3/5/2017 10:36 66
28/4/2017 21:16 66	30/4/2017 10:21 65	30/4/2017 19:26 65	1/5/2017 12:31 65	1/5/2017 21:36 64	3/5/2017 10:41 66
28/4/2017 21:21 65	30/4/2017 10:26 66	30/4/2017 19:31 65	1/5/2017 12:36 65	1/5/2017 21:41 65	3/5/2017 10:46 66
28/4/2017 21:26 66	30/4/2017 10:31 66	30/4/2017 19:36 65	1/5/2017 12:41 66	1/5/2017 21:46 64	3/5/2017 10:51 66
28/4/2017 21:31 66	30/4/2017 10:36 66	30/4/2017 19:41 65	1/5/2017 12:46 65	1/5/2017 21:51 65	3/5/2017 10:56 65
28/4/2017 21:36 65	30/4/2017 10:41 66	30/4/2017 19:46 65	1/5/2017 12:51 65	1/5/2017 21:56 65	3/5/2017 11:01 66
28/4/2017 21:41 66	30/4/2017 10:46 46	30/4/2017 19:51 66	1/5/2017 12:56 66	1/5/2017 22:01 66	3/5/2017 11:06 66
28/4/2017 21:46 65	30/4/2017 10:51 66	30/4/2017 19:56 65	1/5/2017 13:01 65	1/5/2017 22:06 64	3/5/2017 11:11 66
28/4/2017 21:51 66	30/4/2017 10:56 49	30/4/2017 20:01 65	1/5/2017 13:06 66	1/5/2017 22:11 65	3/5/2017 11:16 66
28/4/2017 21:56 66	30/4/2017 11:01 66	30/4/2017 20:06 65	1/5/2017 13:11 65	1/5/2017 22:16 65	3/5/2017 11:21 66
28/4/2017 22:01 66	30/4/2017 11:06 66	30/4/2017 20:11 65	1/5/2017 13:16 65	1/5/2017 22:21 66	3/5/2017 11:26 65
28/4/2017 22:06 65	30/4/2017 11:11 66	30/4/2017 20:16 65	1/5/2017 13:21 65	1/5/2017 22:26 64	3/5/2017 11:31 65
28/4/2017 22:11 66	30/4/2017 11:16 66	30/4/2017 20:21 65	1/5/2017 13:26 65	1/5/2017 22:31 66	3/5/2017 11:36 65
28/4/2017 22:16 66	30/4/2017 11:21 66	30/4/2017 20:26 65	1/5/2017 13:31 65	1/5/2017 22:36 65	3/5/2017 11:41 66
28/4/2017 22:21 65	30/4/2017 11:26 66	30/4/2017 20:31 65	1/5/2017 13:36 66	1/5/2017 22:41 65	3/5/2017 11:46 66
28/4/2017 22:26 65	30/4/2017 11:31 65	30/4/2017 20:36 64	1/5/2017 13:41 66	1/5/2017 22:46 64	3/5/2017 11:51 65
28/4/2017 22:31 66	30/4/2017 11:36 66	30/4/2017 20:41 66	1/5/2017 13:46 65	1/5/2017 22:51 64	3/5/2017 11:56 66
28/4/2017 22:36 66	30/4/2017 11:41 58	30/4/2017 20:46 65	1/5/2017 13:51 65	1/5/2017 22:56 64	3/5/2017 12:01 66
28/4/2017 22:41 66	30/4/2017 11:46 58	30/4/2017 20:51 64	1/5/2017 13:56 65	2/5/2017 19:01 66	3/5/2017 12:06 66
28/4/2017 22:46 66	30/4/2017 11:51 66	30/4/2017 20:56 66	1/5/2017 14:01 65	2/5/2017 19:06 66	3/5/2017 12:11 65
28/4/2017 22:51 65	30/4/2017 11:56 66	30/4/2017 21:01 64	1/5/2017 14:06 65	2/5/2017 19:11 66	3/5/2017 12:16 65
28/4/2017 22:56 66	30/4/2017 12:01 66	30/4/2017 21:06 66	1/5/2017 14:11 66	2/5/2017 19:16 65	3/5/2017 12:21 65
29/4/2017 19:01 66	30/4/2017 12:06 65	30/4/2017 21:11 65	1/5/2017 14:16 66	2/5/2017 19:21 66	3/5/2017 12:26 65
29/4/2017 19:06 66	30/4/2017 12:11 65	30/4/2017 21:16 65	1/5/2017 14:21 65	2/5/2017 19:26 65	3/5/2017 12:31 66
29/4/2017 19:11 66	30/4/2017 12:16 65	30/4/2017 21:21 65	1/5/2017 14:26 65	2/5/2017 19:31 66	3/5/2017 12:36 66
29/4/2017 19:16 65	30/4/2017 12:21 66	30/4/2017 21:26 65	1/5/2017 14:31 66	2/5/2017 19:36 67	3/5/2017 12:41 66
29/4/2017 19:21 66	30/4/2017 12:26 66	30/4/2017 21:31 65	1/5/2017 14:36 54	2/5/2017 19:41 66	3/5/2017 12:46 65
29/4/2017 19:26 66	30/4/2017 12:31 65	30/4/2017 21:36 65	1/5/2017 14:41 66	2/5/2017 19:46 65	3/5/2017 12:51 66
29/4/2017 19:31 66	30/4/2017 12:36 65	30/4/2017 21:41 65	1/5/2017 14:46 65	2/5/2017 19:51 66	3/5/2017 12:56 65
29/4/2017 19:36 66	30/4/2017 12:41 66	30/4/2017 21:46 65	1/5/2017 14:51 65	2/5/2017 19:56 66	3/5/2017 13:01 66
29/4/2017 19:41 66	30/4/2017 12:46 66	30/4/2017 21:51 65	1/5/2017 14:56 65	2/5/2017 20:01 54	3/5/2017 13:06 66
29/4/2017 19:46 65	30/4/2017 12:51 66	30/4/2017 21:56 66	1/5/2017 15:01 65	2/5/2017 20:06 66	3/5/2017 13:11 66
29/4/2017 19:51 66	30/4/2017 12:56 65	30/4/2017 22:01 65	1/5/2017 15:06 66	2/5/2017 20:11 65	3/5/2017 13:16 65
29/4/2017 19:56 66	30/4/2017 13:01 66	30/4/2017 22:06 65	1/5/2017 15:11 66	2/5/2017 20:16 65	3/5/2017 13:21 65
29/4/2017 20:01 56	30/4/2017 13:06 66	30/4/2017 22:11 65	1/5/2017 15:16 65	2/5/2017 20:21 66	3/5/2017 13:26 65
29/4/2017 20:06 65	30/4/2017 13:11 66	30/4/2017 22:16 65	1/5/2017 15:21 66	2/5/2017 20:26 65	3/5/2017 13:31 65
29/4/2017 20:11 66	30/4/2017 13:16 65	30/4/2017 22:21 65	1/5/2017 15:26 65	2/5/2017 20:31 65	3/5/2017 13:36 66
29/4/2017 20:16 65	30/4/2017 13:21 66	30/4/2017 22:26 48	1/5/2017 15:31 64	2/5/2017 20:36 65	3/5/2017 13:41 65
29/4/2017 20:21 65	30/4/2017 13:26 65	30/4/2017 22:31 65	1/5/2017 15:36 65	2/5/2017 20:41 65	3/5/2017 13:46 66
29/4/2017 20:26 65	30/4/2017 13:31 66	30/4/2017 22:36 65	1/5/2017 15:41 65	2/5/2017 20:46 66	3/5/2017 13:51 66
29/4/2017 20:31 65	30/4/2017 13:36 66	30/4/2017 22:41 65	1/5/2017 15:46 65	2/5/2017 20:51 65	3/5/2017 13:56 65
29/4/2017 20:36 66	30/4/2017 13:41 66	30/4/2017 22:46 65	1/5/2017 15:51 66	2/5/2017 20:56 66	3/5/2017 14:01 66
29/4/2017 20:41 66	30/4/2017 13:46 66	30/4/2017 22:51 65	1/5/2017 15:56 65	2/5/2017 21:01 65	3/5/2017 14:06 65
29/4/2017 20:46 65	30/4/2017 13:51 66	30/4/2017 22:56 65	1/5/2017 16:01 65	2/5/2017 21:06 65	3/5/2017 14:11 66
29/4/2017 20:51 66	30/4/2017 13:56 66	1/5/2017 7:01 63	1/5/2017 16:06 65	2/5/2017 21:11 66	3/5/2017 14:16 65
29/4/2017 20:56 65	30/4/2017 14:01 65	1/5/2017 7:06 64	1/5/2017 16:11 65	2/5/2017 21:16 66	3/5/2017 14:21 66
29/4/2017 21:01 65	30/4/2017 14:06 47	1/5/2017 7:11 64	1/5/2017 16:16 65	2/5/2017 21:21 65	3/5/2017 14:26 66
29/4/2017 21:06 66	30/4/2017 14:11 66	1/5/2017 7:16 63	1/5/2017 16:21 66	2/5/2017 21:26 64	3/5/2017 14:31 65
29/4/2017 21:11 65	30/4/2017 14:16 66	1/5/2017 7:21 56	1/5/2017 16:26 66	2/5/2017 21:31 66	3/5/2017 14:36 65
29/4/2017 21:16 66	30/4/2017 14:21 65	1/5/2017 7:26 64	1/5/2017 16:31 65	2/5/2017 21:36 65	3/5/2017 14:41 65
29/4/2017 21:21 53	30/4/2017 14:26 65	1/5/2017 7:31 64	1/5/2017 16:36 66	2/5/2017 21:41 65	3/5/2017 14:46 65
29/4/2017 21:26 65	30/4/2017 14:31 66	1/5/2017 7:36 64	1/5/2017 16:41 65	2/5/2017 21:46 65	3/5/2017 14:51 65
29/4/2017 21:31 65	30/4/2017 14:36 66	1/5/2017 7:41 64	1/5/2017 16:46 65	2/5/2017 21:51 66	3/5/2017 14:56 65
29/4/2017 21:36 66	30/4/2017 14:41 66	1/5/2017 7:46 65	1/5/2017 16:51 66	2/5/2017 21:56 65	3/5/2017 15:01 66
29/4/2017 21:41 65	30/4/2017 14:46 66	1/5/2017 7:51 64	1/5/2017 16:56 66	2/5/2017 22:01 65	3/5/2017 15:06 65
29/4/2017 21:46 65	30/4/2017 14:51 65	1/5/2017 7:56 65	1/5/2017 17:01 65	2/5/2017 22:06 65	3/5/2017 15:11 66
29/4/2017 21:51 65	30/4/2017 14:56 66	1/5/2017 8:01 65	1/5/2017 17:06 66	2/5/2017 22:11 65	3/5/2017 15:16 65
29/4/2017 21:56 66	30/4/2017 15:01 66	1/5/2017 8:06 66	1/5/2017 17:11 66	2/5/2017 22:16 56	3/5/2017 15:21 65
29/4/2017 22:01 65	30/4/2017 15:06 66	1/5/2017 8:11 64	1/5/2017 17:16 65	2/5/2017 22:21 65	3/5/2017 15:26 65
29/4/2017 22:06 66	30/4/2017 15:11 66	1/5/2017 8:16 65	1/5/2017 17:21 66	2/5/2017 22:26 65	3/5/2017 15:31 65
29/4/2017 22:11 65	30/4/2017 15:16 65	1/5/2017 8:21 65	1/5/2017 17:26 66	2/5/2017 22:31 65	3/5/2017 15:36 66
29/4/2017 22:16 65	30/4/2017 15:21 66	1/5/2017 8:26 65	1/5/2017 17:31 66	2/5/2017 22:36 66	3/5/2017 15:41 65
29/4/2017 22:21 65	30/4/2017 15:26 66	1/5/2017 8:31 65	1/5/2017 17:36 66	2/5/2017 22:41 65	3/5/2017 15:46 65
29/4/2017 22:26 65	30/4/2017 15:31 66	1/5/2017 8:36 64	1/5/2017 17:41 66	2/5/2017 22:46 65	3/5/2017 15:51 66
29/4/2017 22:31 65	30/4/2017 15:36 66	1/5/2017 8:41 66	1/5/2017 17:46 66	2/5/2017 22:51 65	3/5/2017 15:56 65
29/4/2017 22:36 66	30/4/2017 15:41 66	1/5/2017 8:46 65	1/5/2017 17:51 66	2/5/2017 22:56 65	3/5/2017 16:01 65
29/4/2017 22:41 66	30/4/2017 15:46 66	1/5/2017 8:51 65	1/5/2017 17:56 65	3/5/2017 7:01 65	3/5/2017 16:06 65
29/4/2017 22:46 65	30/4/2017 15:51 66	1/5/2017 8:56 54	1/5/2017 18:01 66	3/5/2017 7:06 65	3/5/2017 16:11 65
29/4/2017 22:51 66	30/4/2017 15:56 66	1/5/2017 9:01 65	1/5/2017 18:06 66	3/5/2017 7:11 64	3/5/2017 16:16 66
29/4/2017 22:56 65	30/4/2017 16:01 66	1/5/2017 9:06 60	1/5/2017 18:11 65	3/5/2017 7:16 65	3/5/2017 16:21 66
30/4/2017 7:01 64	30/4/2017 16:06 50	1/5/2017 9:11 66	1/5/2017 18:16 65	3/5/2017 7:21 64	3/5/2017 16:26 65
30/4/2017 7:06 64	30/4/2017 16:11 51	1/5/2017 9:16 65	1/5/2017 18:21 60	3/5/2017 7:26 64	3/5/2017 16:31 65
30/4/2017 7:11 66	30/4/2017 16:16 59	1/5/2017 9:21 66	1/5/2017 18:26 66	3/5/2017 7:31 64	3/5/2017 16:36 65
30/4/2017 7:16 64	30/4/2017 16:21 66	1/5/2017 9:26 66	1/5/2017 18:31 65	3/5/2017 7:36 64	3/5/2017 16:41 65
30/4/2017 7:21 64	30/4/2017 16:26 66	1/5/2017 9:31 65	1/5/2017 18:36 66	3/5/2017 7:41 65	3/5/2017 16:46 65
30/4/2017 7:26 64	30/4/2017 16:31 66	1/5/2017 9:36 66	1/5/2017 18:41 66	3/5/2017 7:46 65	3/5/2017 16:51 65
30/4/2017 7:31 64	30/4/2017 16:36 66	1/5/2017 9:41 66	1/5/2017 18:46 66	3/5/2017 7:51 65	3/5/2017 16:56 66
30/4/2017 7:36 64	30/4/2017 16:41 66	1/5/2017 9:46 66	1/5/2017 18:51 66	3/5/2017 7:56 65	3/5/2017 17:01 65
30/4/2017 7:41 65	30/4/2017 16:46 66	1/5/2017 9:51 65	1/5/2017 18:56 66	3/5/2017 8:01 65	3/5/2017 17:06 66
30/4/2017 7:46 56	30/4/2017 16:51 65	1/5/2017 9:56 66	1/5/2017 19:01 65	3/5/2017 8:06 65	3/5/2017 17:11 65
30/4/2017 7:51 64	30/4/2017 16:56 66	1/5/2017 10:01 65	1/5/2017 19:06 65	3/5/2017 8:11 65	3/5/2017 17:16 66
30/4/2017 7:56 66	30/4/2017 17:01 66	1/5/2017 10:06 65	1/5/2017 19:11 65	3/5/2017 8:16 66	3/5/2017 17:21 65
30/4/2017 8:01 65	30/4/2017 17:06 65	1/5/2017 10:11 66	1/5/2017 19:16 65	3/5/2017 8:21 66	3/5/2017 17:26 65
30/4/2017 8:06 64	30/4/2017 17:11 66	1/5/2017 10:16 65	1/5/2017 19:21 66	3/5/2017 8:26 65	3/5/2017 17:31 66
30/4/2017 8:11 64	30/4/2017 17:16 66	1/5/2017 10:21 65	1/5/2017 19:26 65	3/5/2017 8:31 65	3/5/2017 17:36 65
30/4/2017 8:16 65	30/4/2017 17:21 53	1/5/2017 10:26 65	1/5/2017 19:31 65	3/5/2017 8:36 65	3/5/2017 17:41 65
30/4/2017 8:21 65	30/4/2017 17:26 65	1/5/2017 10:31 66	1/5/2017 19:36 65	3/5/2017 8:41 65	3/5/2017 17:46 66
30/4/2017 8:26 65	30/4/2017 17:31 56	1/5/2017 10:36 66	1/5/2017 19:41 65		

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
3/5/2017 19:31	65	5/5/2017 20:36	65	7/5/2017 9:41	65	7/5/2017 18:46	66	9/5/2017 19:51	66	11/5/2017 20:56	65
3/5/2017 19:36	65	5/5/2017 20:41	65	7/5/2017 9:46	66	7/5/2017 18:51	66	9/5/2017 19:56	66	11/5/2017 21:01	65
3/5/2017 19:41	65	5/5/2017 20:46	66	7/5/2017 9:51	66	7/5/2017 18:56	66	9/5/2017 20:01	65	11/5/2017 21:06	66
3/5/2017 19:46	66	5/5/2017 20:51	65	7/5/2017 9:56	66	7/5/2017 19:01	66	9/5/2017 20:06	66	11/5/2017 21:11	65
3/5/2017 19:51	65	5/5/2017 20:56	66	7/5/2017 10:01	66	7/5/2017 19:06	66	9/5/2017 20:11	66	11/5/2017 21:16	65
3/5/2017 19:56	65	5/5/2017 21:01	66	7/5/2017 10:06	59	7/5/2017 19:11	66	9/5/2017 20:16	66	11/5/2017 21:21	65
3/5/2017 20:01	65	5/5/2017 21:06	66	7/5/2017 10:11	57	7/5/2017 19:16	66	9/5/2017 20:21	65	11/5/2017 21:26	65
3/5/2017 20:06	65	5/5/2017 21:11	66	7/5/2017 10:16	66	7/5/2017 19:21	66	9/5/2017 20:26	65	11/5/2017 21:31	66
3/5/2017 20:11	64	5/5/2017 21:16	58	7/5/2017 10:21	66	7/5/2017 19:26	66	9/5/2017 20:31	65	11/5/2017 21:36	65
3/5/2017 20:16	65	5/5/2017 21:21	65	7/5/2017 10:26	66	7/5/2017 19:31	65	9/5/2017 20:36	65	11/5/2017 21:41	65
3/5/2017 20:21	65	5/5/2017 21:26	65	7/5/2017 10:31	61	7/5/2017 19:36	65	9/5/2017 20:41	65	11/5/2017 21:46	65
3/5/2017 20:26	65	5/5/2017 21:31	65	7/5/2017 10:36	49	7/5/2017 19:41	66	9/5/2017 20:46	64	11/5/2017 21:51	65
3/5/2017 20:31	64	5/5/2017 21:36	65	7/5/2017 10:41	66	7/5/2017 19:46	66	9/5/2017 20:51	65	11/5/2017 21:56	66
3/5/2017 20:36	64	5/5/2017 21:41	65	7/5/2017 10:46	66	7/5/2017 19:51	65	9/5/2017 20:56	66	11/5/2017 22:01	65
3/5/2017 20:41	64	5/5/2017 21:46	65	7/5/2017 10:51	66	7/5/2017 19:56	65	9/5/2017 21:01	65	11/5/2017 22:06	66
3/5/2017 20:46	65	5/5/2017 21:51	65	7/5/2017 10:56	66	7/5/2017 20:01	65	9/5/2017 21:06	66	11/5/2017 22:11	65
3/5/2017 20:51	64	5/5/2017 21:56	65	7/5/2017 11:01	58	7/5/2017 20:06	66	9/5/2017 21:11	66	11/5/2017 22:16	66
3/5/2017 20:56	64	5/5/2017 22:01	65	7/5/2017 11:06	66	7/5/2017 20:11	65	9/5/2017 21:16	66	11/5/2017 22:21	65
3/5/2017 21:01	65	5/5/2017 22:06	65	7/5/2017 11:11	66	7/5/2017 20:16	65	9/5/2017 21:21	65	11/5/2017 22:26	66
3/5/2017 21:06	65	5/5/2017 22:11	66	7/5/2017 11:16	66	7/5/2017 20:21	65	9/5/2017 21:26	66	11/5/2017 22:31	66
3/5/2017 21:11	64	5/5/2017 22:16	61	7/5/2017 11:21	47	7/5/2017 20:26	56	9/5/2017 21:31	64	11/5/2017 22:36	66
3/5/2017 21:16	64	5/5/2017 22:21	65	7/5/2017 11:26	47	7/5/2017 20:31	65	9/5/2017 21:36	66	11/5/2017 22:41	66
3/5/2017 21:21	65	5/5/2017 22:26	66	7/5/2017 11:31	52	7/5/2017 20:36	65	9/5/2017 21:41	66	11/5/2017 22:46	66
3/5/2017 21:26	64	5/5/2017 22:31	66	7/5/2017 11:36	66	7/5/2017 20:41	65	9/5/2017 21:46	66	11/5/2017 22:51	66
3/5/2017 21:31	64	5/5/2017 22:36	65	7/5/2017 11:41	66	7/5/2017 20:46	65	9/5/2017 21:51	65	11/5/2017 22:56	65
3/5/2017 21:36	65	5/5/2017 22:41	65	7/5/2017 11:46	54	7/5/2017 20:51	65	9/5/2017 21:56	65	12/5/2017 19:01	65
3/5/2017 21:41	64	5/5/2017 22:46	65	7/5/2017 11:51	47	7/5/2017 20:56	65	9/5/2017 22:01	65	12/5/2017 19:06	65
3/5/2017 21:46	64	5/5/2017 22:51	66	7/5/2017 11:56	66	7/5/2017 21:01	43	9/5/2017 22:06	65	12/5/2017 19:11	65
3/5/2017 21:51	65	5/5/2017 22:56	66	7/5/2017 12:01	63	7/5/2017 21:06	66	9/5/2017 22:11	65	12/5/2017 19:16	65
3/5/2017 21:56	65	6/5/2017 19:01	66	7/5/2017 12:06	52	7/5/2017 21:11	65	9/5/2017 22:16	65	12/5/2017 19:21	65
3/5/2017 22:01	65	6/5/2017 19:06	65	7/5/2017 12:11	51	7/5/2017 21:16	65	9/5/2017 22:21	66	12/5/2017 19:26	65
3/5/2017 22:06	64	6/5/2017 19:11	66	7/5/2017 12:16	66	7/5/2017 21:21	66	9/5/2017 22:26	65	12/5/2017 19:31	65
3/5/2017 22:11	64	6/5/2017 19:16	66	7/5/2017 12:21	52	7/5/2017 21:26	66	9/5/2017 22:31	65	12/5/2017 19:36	65
3/5/2017 22:16	66	6/5/2017 19:21	66	7/5/2017 12:26	66	7/5/2017 21:31	65	9/5/2017 22:36	62	12/5/2017 19:41	65
3/5/2017 22:21	64	6/5/2017 19:26	66	7/5/2017 12:31	55	7/5/2017 21:36	66	9/5/2017 22:41	66	12/5/2017 19:46	66
3/5/2017 22:26	64	6/5/2017 19:31	66	7/5/2017 12:36	59	7/5/2017 21:41	66	9/5/2017 22:46	65	12/5/2017 19:51	66
3/5/2017 22:31	65	6/5/2017 19:36	65	7/5/2017 12:41	66	7/5/2017 21:46	65	9/5/2017 22:51	65	12/5/2017 19:56	66
3/5/2017 22:36	64	6/5/2017 19:41	66	7/5/2017 12:46	51	7/5/2017 21:51	65	9/5/2017 22:56	66	12/5/2017 20:01	65
3/5/2017 22:41	65	6/5/2017 19:46	66	7/5/2017 12:51	66	7/5/2017 21:56	65	10/5/2017 19:01	66	12/5/2017 20:06	65
3/5/2017 22:46	64	6/5/2017 19:51	66	7/5/2017 12:56	66	7/5/2017 22:01	65	10/5/2017 19:06	66	12/5/2017 20:11	66
3/5/2017 22:51	66	6/5/2017 19:56	65	7/5/2017 13:01	66	7/5/2017 22:06	65	10/5/2017 19:11	66	12/5/2017 20:16	66
3/5/2017 22:56	64	6/5/2017 20:01	66	7/5/2017 13:06	66	7/5/2017 22:11	65	10/5/2017 19:16	66	12/5/2017 20:21	65
4/5/2017 19:01	66	6/5/2017 20:06	65	7/5/2017 13:11	55	7/5/2017 22:16	65	10/5/2017 19:21	65	12/5/2017 20:26	66
4/5/2017 19:06	66	6/5/2017 20:11	66	7/5/2017 13:16	55	7/5/2017 22:21	65	10/5/2017 19:26	66	12/5/2017 20:31	65
4/5/2017 19:11	66	6/5/2017 20:16	55	7/5/2017 13:21	62	7/5/2017 22:26	65	10/5/2017 19:31	66	12/5/2017 20:36	65
4/5/2017 19:16	66	6/5/2017 20:21	66	7/5/2017 13:26	53	7/5/2017 22:31	65	10/5/2017 19:36	66	12/5/2017 20:41	65
4/5/2017 19:21	65	6/5/2017 20:26	66	7/5/2017 13:31	62	7/5/2017 22:36	64	10/5/2017 19:41	66	12/5/2017 20:46	64
4/5/2017 19:26	66	6/5/2017 20:31	65	7/5/2017 13:36	57	7/5/2017 22:41	65	10/5/2017 19:46	66	12/5/2017 20:51	65
4/5/2017 19:31	66	6/5/2017 20:36	65	7/5/2017 13:41	61	7/5/2017 22:46	65	10/5/2017 19:51	65	12/5/2017 20:56	64
4/5/2017 19:36	66	6/5/2017 20:41	65	7/5/2017 13:46	66	7/5/2017 22:51	64	10/5/2017 19:56	66	12/5/2017 21:01	65
4/5/2017 19:41	66	6/5/2017 20:46	65	7/5/2017 13:51	66	7/5/2017 22:56	64	10/5/2017 20:01	65	12/5/2017 21:06	65
4/5/2017 19:46	66	6/5/2017 20:51	66	7/5/2017 13:56	66	8/5/2017 19:01	68	10/5/2017 20:06	65	12/5/2017 21:11	64
4/5/2017 19:51	66	6/5/2017 20:56	65	7/5/2017 14:01	66	8/5/2017 19:06	57	10/5/2017 20:11	65	12/5/2017 21:16	64
4/5/2017 19:56	65	6/5/2017 21:01	66	7/5/2017 14:06	66	8/5/2017 19:11	58	10/5/2017 20:16	65	12/5/2017 21:21	64
4/5/2017 20:01	66	6/5/2017 21:06	65	7/5/2017 14:11	66	8/5/2017 19:16	53	10/5/2017 20:21	61	12/5/2017 21:26	64
4/5/2017 20:06	66	6/5/2017 21:11	65	7/5/2017 14:16	66	8/5/2017 19:21	66	10/5/2017 20:26	66	12/5/2017 21:31	64
4/5/2017 20:11	65	6/5/2017 21:16	65	7/5/2017 14:21	66	8/5/2017 19:26	55	10/5/2017 20:31	66	12/5/2017 21:36	65
4/5/2017 20:16	66	6/5/2017 21:21	65	7/5/2017 14:26	53	8/5/2017 19:31	66	10/5/2017 20:36	66	12/5/2017 21:41	64
4/5/2017 20:21	66	6/5/2017 21:26	66	7/5/2017 14:31	58	8/5/2017 19:36	66	10/5/2017 20:41	66	12/5/2017 21:46	64
4/5/2017 20:26	66	6/5/2017 21:31	65	7/5/2017 14:36	66	8/5/2017 19:41	66	10/5/2017 20:46	53	12/5/2017 21:51	64
4/5/2017 20:31	66	6/5/2017 21:36	66	7/5/2017 14:41	66	8/5/2017 19:46	47	10/5/2017 20:51	66	12/5/2017 21:56	65
4/5/2017 20:36	66	6/5/2017 21:41	65	7/5/2017 14:46	66	8/5/2017 19:51	66	10/5/2017 20:56	65	12/5/2017 22:01	64
4/5/2017 20:41	66	6/5/2017 21:46	65	7/5/2017 14:51	66	8/5/2017 19:56	66	10/5/2017 21:01	65	12/5/2017 22:06	65
4/5/2017 20:46	66	6/5/2017 21:51	66	7/5/2017 14:56	66	8/5/2017 20:01	66	10/5/2017 21:06	65	12/5/2017 22:11	64
4/5/2017 20:51	65	6/5/2017 21:56	66	7/5/2017 15:01	66	8/5/2017 20:06	66	10/5/2017 21:11	65	12/5/2017 22:16	65
4/5/2017 20:56	66	6/5/2017 22:01	65	7/5/2017 15:06	66	8/5/2017 20:11	66	10/5/2017 21:16	65	12/5/2017 22:21	65
4/5/2017 21:01	65	6/5/2017 22:06	66	7/5/2017 15:11	59	8/5/2017 20:16	66	10/5/2017 21:21	66	12/5/2017 22:26	65
4/5/2017 21:06	65	6/5/2017 22:11	66	7/5/2017 15:16	66	8/5/2017 20:21	66	10/5/2017 21:26	66	12/5/2017 22:31	65
4/5/2017 21:11	65	6/5/2017 22:16	65	7/5/2017 15:21	66	8/5/2017 20:26	66	10/5/2017 21:31	65	12/5/2017 22:36	65
4/5/2017 21:16	65	6/5/2017 22:21	49	7/5/2017 15:26	66	8/5/2017 20:31	65	10/5/2017 21:36	65	12/5/2017 22:41	65
4/5/2017 21:21	65	6/5/2017 22:26	65	7/5/2017 15:31	52	8/5/2017 20:36	66	10/5/2017 21:41	65	12/5/2017 22:46	64
4/5/2017 21:26	65	6/5/2017 22:31	65	7/5/2017 15:36	66	8/5/2017 20:41	66	10/5/2017 21:46	66	12/5/2017 22:51	65
4/5/2017 21:31	65	6/5/2017 22:36	65	7/5/2017 15:41	66	8/5/2017 20:46	66	10/5/2017 21:51	66	12/5/2017 22:56	64
4/5/2017 21:36	65	6/5/2017 22:41	67	7/5/2017 15:46	53	8/5/2017 20:51	66	10/5/2017 21:56	66	13/5/2017 19:01	62
4/5/2017 21:41	65	6/5/2017 22:46	65	7/5/2017 15:51	66	8/5/2017 20:56	66	10/5/2017 22:01	66	13/5/2017 19:06	62
4/5/2017 21:46	65	6/5/201									

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)					
13/5/2017 22:01	66	14/5/2017 15:06	52	15/5/2017 20:11	66	17/5/2017 21:16	65
13/5/2017 22:06	65	14/5/2017 15:11	52	15/5/2017 20:16	65	17/5/2017 21:21	65
13/5/2017 22:11	66	14/5/2017 15:16	52	15/5/2017 20:21	65	17/5/2017 21:26	65
13/5/2017 22:16	65	14/5/2017 15:21	66	15/5/2017 20:26	66	17/5/2017 21:31	65
13/5/2017 22:21	66	14/5/2017 15:26	66	15/5/2017 20:31	66	17/5/2017 21:36	65
13/5/2017 22:26	65	14/5/2017 15:31	66	15/5/2017 20:36	65	17/5/2017 21:41	65
13/5/2017 22:31	66	14/5/2017 15:36	66	15/5/2017 20:41	65	17/5/2017 21:46	65
13/5/2017 22:36	66	14/5/2017 15:41	66	15/5/2017 20:46	65	17/5/2017 21:51	65
13/5/2017 22:41	66	14/5/2017 15:46	66	15/5/2017 20:51	65	17/5/2017 21:56	65
13/5/2017 22:46	66	14/5/2017 15:51	53	15/5/2017 20:56	65	17/5/2017 22:01	65
13/5/2017 22:51	66	14/5/2017 15:56	66	15/5/2017 21:01	65	17/5/2017 22:06	65
13/5/2017 22:56	65	14/5/2017 16:01	66	15/5/2017 21:06	65	17/5/2017 22:11	66
14/5/2017 7:01	63	14/5/2017 16:06	66	15/5/2017 21:11	65	17/5/2017 22:16	65
14/5/2017 7:06	64	14/5/2017 16:11	66	15/5/2017 21:16	65	17/5/2017 22:21	66
14/5/2017 7:11	63	14/5/2017 16:16	66	15/5/2017 21:21	66	17/5/2017 22:26	65
14/5/2017 7:16	64	14/5/2017 16:21	66	15/5/2017 21:26	65	17/5/2017 22:31	66
14/5/2017 7:21	64	14/5/2017 16:26	66	15/5/2017 21:31	65	17/5/2017 22:36	65
14/5/2017 7:26	64	14/5/2017 16:31	54	15/5/2017 21:36	65	17/5/2017 22:41	66
14/5/2017 7:31	64	14/5/2017 16:36	66	15/5/2017 21:41	65	17/5/2017 22:46	65
14/5/2017 7:36	64	14/5/2017 16:41	66	15/5/2017 21:46	66	17/5/2017 22:51	65
14/5/2017 7:41	65	14/5/2017 16:46	66	15/5/2017 21:51	66	17/5/2017 22:56	65
14/5/2017 7:46	65	14/5/2017 16:51	66	15/5/2017 21:56	65	18/5/2017 19:01	65
14/5/2017 7:51	66	14/5/2017 16:56	66	15/5/2017 22:01	66	18/5/2017 19:06	64
14/5/2017 7:56	65	14/5/2017 17:01	66	15/5/2017 22:06	58	18/5/2017 19:11	65
14/5/2017 8:01	66	14/5/2017 17:06	66	15/5/2017 22:11	65	18/5/2017 19:16	65
14/5/2017 8:06	65	14/5/2017 17:11	66	15/5/2017 22:16	66	18/5/2017 19:21	65
14/5/2017 8:11	65	14/5/2017 17:16	66	15/5/2017 22:21	65	18/5/2017 19:26	65
14/5/2017 8:16	66	14/5/2017 17:21	66	15/5/2017 22:26	65	18/5/2017 19:31	54
14/5/2017 8:21	65	14/5/2017 17:26	66	15/5/2017 22:31	65	18/5/2017 19:36	66
14/5/2017 8:26	56	14/5/2017 17:31	66	15/5/2017 22:36	65	18/5/2017 19:41	66
14/5/2017 8:31	66	14/5/2017 17:36	66	15/5/2017 22:41	65	18/5/2017 19:46	66
14/5/2017 8:36	65	14/5/2017 17:41	66	15/5/2017 22:46	65	18/5/2017 19:51	66
14/5/2017 8:41	66	14/5/2017 17:46	66	15/5/2017 22:51	65	18/5/2017 19:56	66
14/5/2017 8:46	66	14/5/2017 17:51	66	15/5/2017 22:56	65	18/5/2017 20:01	66
14/5/2017 8:51	66	14/5/2017 17:56	66	16/5/2017 19:01	66	18/5/2017 20:06	65
14/5/2017 8:56	65	14/5/2017 18:01	66	16/5/2017 19:06	66	18/5/2017 20:11	66
14/5/2017 9:01	66	14/5/2017 18:06	66	16/5/2017 19:11	66	18/5/2017 20:16	66
14/5/2017 9:06	66	14/5/2017 18:11	66	16/5/2017 19:16	66	18/5/2017 20:21	66
14/5/2017 9:11	66	14/5/2017 18:16	66	16/5/2017 19:21	66	18/5/2017 20:26	65
14/5/2017 9:16	66	14/5/2017 18:21	66	16/5/2017 19:26	65	18/5/2017 20:31	65
14/5/2017 9:21	66	14/5/2017 18:26	65	16/5/2017 19:31	66	18/5/2017 20:36	65
14/5/2017 9:26	66	14/5/2017 18:31	66	16/5/2017 19:36	65	18/5/2017 20:41	66
14/5/2017 9:31	66	14/5/2017 18:36	65	16/5/2017 19:41	66	18/5/2017 20:46	66
14/5/2017 9:36	66	14/5/2017 18:41	66	16/5/2017 19:46	66	18/5/2017 20:51	66
14/5/2017 9:41	66	14/5/2017 18:46	65	16/5/2017 19:51	66	18/5/2017 20:56	66
14/5/2017 9:46	66	14/5/2017 18:51	66	16/5/2017 19:56	66	18/5/2017 21:01	66
14/5/2017 9:51	66	14/5/2017 18:56	65	16/5/2017 20:01	66	18/5/2017 21:06	65
14/5/2017 9:56	56	14/5/2017 19:01	66	16/5/2017 20:06	66	18/5/2017 21:11	66
14/5/2017 10:01	66	14/5/2017 19:06	65	16/5/2017 20:11	65	18/5/2017 21:16	66
14/5/2017 10:06	66	14/5/2017 19:11	66	16/5/2017 20:16	66	18/5/2017 21:21	65
14/5/2017 10:11	66	14/5/2017 19:16	65	16/5/2017 20:21	66	18/5/2017 21:26	65
14/5/2017 10:16	65	14/5/2017 19:21	65	16/5/2017 20:26	65	18/5/2017 21:31	66
14/5/2017 10:21	66	14/5/2017 19:26	65	16/5/2017 20:31	66	18/5/2017 21:36	65
14/5/2017 10:26	66	14/5/2017 19:31	65	16/5/2017 20:36	66	18/5/2017 21:41	66
14/5/2017 10:31	59	14/5/2017 19:36	66	16/5/2017 20:41	66	18/5/2017 21:46	60
14/5/2017 10:36	66	14/5/2017 19:41	65	16/5/2017 20:46	65	18/5/2017 21:51	65
14/5/2017 10:41	66	14/5/2017 19:46	65	16/5/2017 20:51	65	18/5/2017 21:56	66
14/5/2017 10:46	65	14/5/2017 19:51	65	16/5/2017 20:56	66	18/5/2017 22:01	65
14/5/2017 10:51	66	14/5/2017 19:56	65	16/5/2017 21:01	64	18/5/2017 22:06	65
14/5/2017 10:56	65	14/5/2017 20:01	65	16/5/2017 21:06	65	18/5/2017 22:11	65
14/5/2017 11:01	65	14/5/2017 20:06	65	16/5/2017 21:11	65	18/5/2017 22:16	65
14/5/2017 11:06	65	14/5/2017 20:11	65	16/5/2017 21:16	66	18/5/2017 22:21	66
14/5/2017 11:11	65	14/5/2017 20:16	65	16/5/2017 21:21	66	18/5/2017 22:26	65
14/5/2017 11:16	65	14/5/2017 20:21	66	16/5/2017 21:26	65	18/5/2017 22:31	65
14/5/2017 11:21	66	14/5/2017 20:26	65	16/5/2017 21:31	64	18/5/2017 22:36	65
14/5/2017 11:26	65	14/5/2017 20:31	65	16/5/2017 21:36	65	18/5/2017 22:41	65
14/5/2017 11:31	65	14/5/2017 20:36	65	16/5/2017 21:41	65	18/5/2017 22:46	66
14/5/2017 11:36	66	14/5/2017 20:41	65	16/5/2017 21:46	65	18/5/2017 22:51	65
14/5/2017 11:41	66	14/5/2017 20:46	64	16/5/2017 21:51	65	18/5/2017 22:56	65
14/5/2017 11:46	65	14/5/2017 20:51	65	16/5/2017 21:56	66	19/5/2017 19:01	66
14/5/2017 11:51	65	14/5/2017 20:56	65	16/5/2017 22:01	66	19/5/2017 19:06	66
14/5/2017 11:56	66	14/5/2017 21:01	64	16/5/2017 22:06	65	19/5/2017 19:11	66
14/5/2017 12:01	66	14/5/2017 21:06	64	16/5/2017 22:11	65	19/5/2017 19:16	66
14/5/2017 12:06	66	14/5/2017 21:11	64	16/5/2017 22:16	66	19/5/2017 19:21	66
14/5/2017 12:11	66	14/5/2017 21:16	65	16/5/2017 22:21	65	19/5/2017 19:26	66
14/5/2017 12:16	66	14/5/2017 21:21	65	16/5/2017 22:26	65	19/5/2017 19:31	66
14/5/2017 12:21	54	14/5/2017 21:26	65	16/5/2017 22:31	66	19/5/2017 19:36	66
14/5/2017 12:26	65	14/5/2017 21:31	65	16/5/2017 22:36	65	19/5/2017 19:41	66
14/5/2017 12:31	66	14/5/2017 21:36	65	16/5/2017 22:41	66	19/5/2017 19:46	66
14/5/2017 12:36	66	14/5/2017 21:41	65	16/5/2017 22:46	65	19/5/2017 19:51	56
14/5/2017 12:41	66	14/5/2017 21:46	65	16/5/2017 22:51	66	19/5/2017 19:56	57
14/5/2017 12:46	66	14/5/2017 21:51	65	16/5/2017 22:56	66	19/5/2017 20:01	51
14/5/2017 12:51	54	14/5/2017 21:56	65	17/5/2017 19:01	66	19/5/2017 20:06	66
14/5/2017 12:56	65	14/5/2017 22:01	60	17/5/2017 19:06	66	19/5/2017 20:11	66
14/5/2017 13:01	66	14/5/2017 22:06	65	17/5/2017 19:11	66	19/5/2017 20:16	55
14/5/2017 13:06	66	14/5/2017 22:11	65	17/5/2017 19:16	65	19/5/2017 20:21	66
14/5/2017 13:11	66	14/5/2017 22:16	65	17/5/2017 19:21	65	19/5/2017 20:26	66
14/5/2017 13:16	66	14/5/2017 22:21	65	17/5/2017 19:26	66	19/5/2017 20:31	59
14/5/2017 13:21	66	14/5/2017 22:26	65	17/5/2017 19:31	66	19/5/2017 20:36	66
14/5/2017 13:26	66	14/5/2017 22:31	65	17/5/2017 19:36	66	19/5/2017 20:41	66
14/5/2017 13:31	66	14/5/2017 22:36	65	17/5/2017 19:41	66	19/5/2017 20:46	66
14/5/2017 13:36	66	14/5/2017 22:41	65	17/5/2017 19:46	66	19/5/2017 20:51	66
14/5/2017 13:41	66	14/5/2017 22:46	65	17/5/2017 19:51	66	19/5/2017 20:56	66
14/5/2017 13:46	65	14/5/2017 22:51	65	17/5/2017 19:56	66	19/5/2017 21:01	65
14/5/2017 13:51	66	14/5/2017 22:56	64	17/5/2017 20:01	65	19/5/2017 21:06	65
14/5/2017 13:56	65	15/5/2017 19:01	66	17/5/2017 20:06	66	19/5/2017 21:11	66
14/5/2017 14:01	65	15/5/2017 19:06	66	17/5/2017 20:11	66	19/5/2017 21:16	66
14/5/2017 14:06	65	15/5/2017 19:11	66	17/5/2017 20:16	66	19/5/2017 21:21	65
14/5/2017 14:11	66	15/5/2017 19:16	65	17/5/2017 20:21	65	19/5/2017 21:26	66
14/5/2017 14:16	66	15/5/2017 19:21	66	17/5/2017 20:26	65	19/5/2017 21:31	66
14/5/2017 14:21	66	15/5/2017 19:26	66	17/5/2017 20:31	66	19/5/2017 21:36	66
14/5/2017 14:26	69	15/5/2017 19:31	66	17/5/2017 20:36	65	19/5/2017 21:41	66
14/5/2017 14:31	66	15/5/2017 19:36	66	17/5/2017 20:41	65	19/5/2017 21:46	66
14/5/2017 14:36	59	15/5/2017 19:41	66	17/5/2017 20:46	66	19/5/2017 21:51	66
14/5/2017 14:41	66	15/5/2017 19:46	66	17/5/2017 20:51	65	19/5/2017 21:56	66
14/5/2017 14:46	66	15/5/2017 19:51	66	17/5/2017 20:56	65	19/5/2017 22:01	66
14/5/2017 14:51	56	15/5/2017 19:56	66	17/5/2017 21:01	66	19/5/2017 22:06	65
14/5/2017 14:56	66	15/5/2017 20:01	66	17/5/2017 21:06	64	19/5/2017 22:11	65
14/5/2017 15:01	48	15/5/2017 20:06	66	17/5/2017 21:11	65	19/5/2017 22:16	

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)											
21/5/2017 20:31	66	23/5/2017 21:36	66	25/5/2017 22:41	65	27/4/2017 4:31	60	28/4/2017 5:36	61	29/4/2017 6:41	60		
21/5/2017 20:36	53	23/5/2017 21:41	66	25/5/2017 22:46	66	27/4/2017 4:36	60	28/4/2017 5:41	62	29/4/2017 6:46	70		
21/5/2017 20:41	66	23/5/2017 21:46	66	25/5/2017 22:51	65	27/4/2017 4:41	60	28/4/2017 5:46	63	29/4/2017 6:51	64		
21/5/2017 20:46	65	23/5/2017 21:51	65	25/5/2017 22:56	65	27/4/2017 4:46	60	28/4/2017 5:51	63	29/4/2017 6:56	64		
21/5/2017 20:51	66	23/5/2017 21:56	66	26/5/2017 19:01	66	27/4/2017 4:51	60	28/4/2017 5:56	52	29/4/2017 7:01	60		
21/5/2017 20:56	66	23/5/2017 22:01	66	26/5/2017 19:06	66	27/4/2017 4:56	60	28/4/2017 6:01	63	29/4/2017 7:06	59		
21/5/2017 21:01	65	23/5/2017 22:06	65	26/5/2017 19:11	66	27/4/2017 5:01	61	28/4/2017 6:06	57	29/4/2017 7:11	60		
21/5/2017 21:06	65	23/5/2017 22:11	66	26/5/2017 19:16	45	27/4/2017 5:06	61	28/4/2017 6:11	53	29/4/2017 7:16	61		
21/5/2017 21:11	66	23/5/2017 22:16	65	26/5/2017 19:21	66	27/4/2017 5:11	61	28/4/2017 6:16	58	29/4/2017 7:21	60		
21/5/2017 21:16	65	23/5/2017 22:21	65	26/5/2017 19:26	66	27/4/2017 5:16	60	28/4/2017 6:21	60	29/4/2017 7:26	60		
21/5/2017 21:21	65	23/5/2017 22:26	65	26/5/2017 19:31	66	27/4/2017 5:21	61	28/4/2017 6:26	60	29/4/2017 7:31	59		
21/5/2017 21:26	65	23/5/2017 22:31	66	26/5/2017 19:36	66	27/4/2017 5:26	61	28/4/2017 6:31	61	29/4/2017 7:36	59		
21/5/2017 21:31	66	23/5/2017 22:36	65	26/5/2017 19:41	40	27/4/2017 5:31	61	28/4/2017 6:36	64	29/4/2017 7:41	58		
21/5/2017 21:36	65	23/5/2017 22:41	66	26/5/2017 19:46	66	27/4/2017 5:36	63	28/4/2017 6:41	63	29/4/2017 7:46	57		
21/5/2017 21:41	65	23/5/2017 22:46	65	26/5/2017 19:51	66	27/4/2017 5:41	62	28/4/2017 6:46	63	29/4/2017 7:51	58		
21/5/2017 21:46	66	23/5/2017 22:51	65	26/5/2017 19:56	65	27/4/2017 5:46	51	28/4/2017 6:51	63	29/4/2017 7:56	61		
21/5/2017 21:51	66	23/5/2017 22:56	66	26/5/2017 20:01	66	27/4/2017 5:51	63	28/4/2017 6:56	64	30/4/2017 0:01	55		
21/5/2017 21:56	66	24/5/2017 19:01	57	26/5/2017 20:06	66	27/4/2017 5:56	62	28/4/2017 7:01	62	30/4/2017 0:06	59		
21/5/2017 22:01	66	24/5/2017 19:06	66	26/5/2017 20:11	65	27/4/2017 6:01	52	28/4/2017 7:06	61	30/4/2017 0:11	58		
21/5/2017 22:06	66	24/5/2017 19:11	66	26/5/2017 20:16	66	27/4/2017 6:06	65	28/4/2017 7:11	62	30/4/2017 0:16	58		
21/5/2017 22:11	66	24/5/2017 19:16	66	26/5/2017 20:21	66	27/4/2017 6:11	61	28/4/2017 7:16	61	30/4/2017 0:21	55		
21/5/2017 22:16	65	24/5/2017 19:21	66	26/5/2017 20:26	66	27/4/2017 6:16	55	28/4/2017 7:21	62	30/4/2017 0:26	60		
21/5/2017 22:21	65	24/5/2017 19:26	66	26/5/2017 20:31	66	27/4/2017 6:21	61	28/4/2017 7:26	63	30/4/2017 0:31	53		
21/5/2017 22:26	65	24/5/2017 19:31	66	26/5/2017 20:36	65	27/4/2017 6:26	62	28/4/2017 7:31	61	30/4/2017 0:36	56		
21/5/2017 22:31	65	24/5/2017 19:36	66	26/5/2017 20:41	65	27/4/2017 6:31	62	28/4/2017 7:36	66	30/4/2017 0:41	49		
21/5/2017 22:36	65	24/5/2017 19:41	66	26/5/2017 20:46	65	27/4/2017 6:36	61	28/4/2017 7:41	60	30/4/2017 0:46	51		
21/5/2017 22:41	66	24/5/2017 19:46	66	26/5/2017 20:51	66	27/4/2017 6:41	62	28/4/2017 7:46	61	30/4/2017 0:51	49		
21/5/2017 22:46	65	24/5/2017 19:51	60	26/5/2017 20:56	66	27/4/2017 6:46	64	28/4/2017 7:51	60	30/4/2017 0:56	64		
21/5/2017 22:51	65	24/5/2017 19:56	66	26/5/2017 21:01	55	27/4/2017 6:51	64	28/4/2017 7:56	61	30/4/2017 1:01	47		
21/5/2017 22:56	64	24/5/2017 20:01	66	26/5/2017 21:06	64	27/4/2017 6:56	67	29/4/2017 0:01	60	30/4/2017 1:06	48		
22/5/2017 19:01	66	24/5/2017 20:06	56	26/5/2017 21:11	65	27/4/2017 7:01	63	29/4/2017 0:06	61	30/4/2017 1:11	63		
22/5/2017 19:06	66	24/5/2017 20:11	65	26/5/2017 21:16	65	27/4/2017 7:06	61	29/4/2017 0:11	60	30/4/2017 1:16	45		
22/5/2017 19:11	66	24/5/2017 20:16	66	26/5/2017 21:21	64	27/4/2017 7:11	61	29/4/2017 0:16	58	30/4/2017 1:21	63		
22/5/2017 19:16	66	24/5/2017 20:21	66	26/5/2017 21:26	65	27/4/2017 7:16	61	29/4/2017 0:21	56	30/4/2017 1:26	51		
22/5/2017 19:21	40	24/5/2017 20:26	66	26/5/2017 21:31	65	27/4/2017 7:21	62	29/4/2017 0:26	63	30/4/2017 1:31	45		
22/5/2017 19:26	55	24/5/2017 20:31	65	26/5/2017 21:36	65	27/4/2017 7:26	62	29/4/2017 0:31	54	30/4/2017 1:36	62		
22/5/2017 19:31	66	24/5/2017 20:36	65	26/5/2017 21:41	65	27/4/2017 7:31	60	29/4/2017 0:36	55	30/4/2017 1:41	62		
22/5/2017 19:36	66	24/5/2017 20:41	66	26/5/2017 21:46	65	27/4/2017 7:36	59	29/4/2017 0:41	58	30/4/2017 1:46	63		
22/5/2017 19:41	66	24/5/2017 20:46	65	26/5/2017 21:51	65	27/4/2017 7:41	61	29/4/2017 0:46	58	30/4/2017 1:51	62		
22/5/2017 19:46	53	24/5/2017 20:51	65	26/5/2017 21:56	58	27/4/2017 7:46	59	29/4/2017 0:51	59	30/4/2017 1:56	62		
22/5/2017 19:51	66	24/5/2017 20:56	66	26/5/2017 22:01	66	27/4/2017 7:51	57	29/4/2017 0:56	55	30/4/2017 2:01	60		
22/5/2017 19:56	66	24/5/2017 21:01	65	26/5/2017 22:06	65	27/4/2017 7:56	59	29/4/2017 1:01	55	30/4/2017 2:06	63		
22/5/2017 20:01	66	24/5/2017 21:06	65	26/5/2017 22:11	57	28/4/2017 0:01	60	29/4/2017 1:06	55	30/4/2017 2:11	63		
22/5/2017 20:06	66	24/5/2017 21:11	65	26/5/2017 22:16	66	28/4/2017 0:06	58	29/4/2017 1:11	52	30/4/2017 2:16	62		
22/5/2017 20:11	66	24/5/2017 21:16	66	26/5/2017 22:21	65	28/4/2017 0:11	57	29/4/2017 1:16	55	30/4/2017 2:21	62		
22/5/2017 20:16	66	24/5/2017 21:21	65	26/5/2017 22:26	66	28/4/2017 0:16	59	29/4/2017 1:21	55	30/4/2017 2:26	62		
22/5/2017 20:21	66	24/5/2017 21:26	65	26/5/2017 22:31	65	28/4/2017 0:21	58	29/4/2017 1:26	59	30/4/2017 2:31	61		
22/5/2017 20:26	66	24/5/2017 21:31	65	26/5/2017 22:36	65	28/4/2017 0:26	55	29/4/2017 1:31	54	30/4/2017 2:36	62		
22/5/2017 20:31	66	24/5/2017 21:36	65	26/5/2017 22:41	65	28/4/2017 0:31	61	29/4/2017 1:36	52	30/4/2017 2:41	62		
22/5/2017 20:36	65	24/5/2017 21:41	65	26/5/2017 22:46	65	28/4/2017 0:36	46	29/4/2017 1:41	48	30/4/2017 2:46	62		
22/5/2017 20:41	66	24/5/2017 21:46	65	26/5/2017 22:51	66	28/4/2017 0:41	57	29/4/2017 1:46	63	30/4/2017 2:51	62		
22/5/2017 20:46	66	24/5/2017 21:51	66	26/5/2017 22:56	65	28/4/2017 0:46	63	29/4/2017 1:51	55	30/4/2017 2:56	61		
22/5/2017 20:51	66	24/5/2017 21:56	65	Night time: 23:00-07:00		28/4/2017 0:51	51	29/4/2017 1:56	56	30/4/2017 3:01	62		
22/5/2017 20:56	66	24/5/2017 22:01	65			28/4/2017 0:56	54	29/4/2017 2:01	62	30/4/2017 3:06	62		
22/5/2017 21:01	65	24/5/2017 22:06	65			28/4/2017 1:01	63	29/4/2017 2:06	51	30/4/2017 3:11	61		
22/5/2017 21:06	65	24/5/2017 22:11	65	27/4/2017 0:01	59	28/4/2017 1:06	63	29/4/2017 2:11	63	30/4/2017 3:16	62		
22/5/2017 21:11	65	24/5/2017 22:16	66	27/4/2017 0:06	60	28/4/2017 1:11	51	29/4/2017 2:16	63	30/4/2017 3:21	62		
22/5/2017 21:16	65	24/5/2017 22:21	66	27/4/2017 0:11	57	28/4/2017 1:16	63	29/4/2017 2:21	48	30/4/2017 3:26	61		
22/5/2017 21:21	66	24/5/2017 22:26	65	27/4/2017 0:16	59	28/4/2017 1:21	63	29/4/2017 2:26	40	30/4/2017 3:31	61		
22/5/2017 21:26	65	24/5/2017 22:31	65	27/4/2017 0:21	55	28/4/2017 1:26	62	29/4/2017 2:31	62	30/4/2017 3:36	61		
22/5/2017 21:31	65	24/5/2017 22:36	65	27/4/2017 0:26	58	28/4/2017 1:31	43	29/4/2017 2:36	62	30/4/2017 3:41	61		
22/5/2017 21:36	65	24/5/2017 22:41	66	27/4/2017 0:31	51	28/4/2017 1:36	62	29/4/2017 2:41	62	30/4/2017 3:46	62		
22/5/2017 21:41	65	24/5/2017 22:46	65	27/4/2017 0:36	56	28/4/2017 1:41	61	29/4/2017 2:46	62	30/4/2017 3:51	61		
22/5/2017 21:46	65	24/5/2017 22:51	65	27/4/2017 0:41	53	28/4/2017 1:46	61	29/4/2017 2:51	62	30/4/2017 3:56	63		
22/5/2017 21:51	65	24/5/2017 22:56	66	27/4/2017 0:46	56	28/4/2017 1:51	62	29/4/2017 2:56	51	30/4/2017 4:01	60		
22/5/2017 21:56	50	25/5/2017 19:01	66	27/4/2017 0:51	48	28/4/2017 1:56	61	29/4/2017 3:01	62	30/4/2017 4:06	60		
22/5/2017 22:01	66	25/5/2017 19:06	66	27/4/2017 0:56	52	28/4/2017 2:01	63	29/4/2017 3:06	62	30/4/2017 4:11	61		
22/5/2017 22:06	65	25/5/2017 19:11	66	27/4/2017 1:01	45	28/4/2017 2:06	61	29/4/2017 3:11	61	30/4/2017 4:16	60		
22/5/2017 22:11	65	25/5/2017 19:16	66	27/4/2017 1:06	63	28/4/2017 2:11	61	29/4/2017 3:16	61	30/4/2017 4:21	61		
22/5/2017 22:16	66	25/5/2017 19:21	66	27/4/2017 1:11	37	28/4/2017 2:16	62	29/4/2017 3:21	62	30/4/2017 4:26	61		
22/5/2017 22:21	64	25/5/2017 19:26	66	27/4/2017 1:16	62	28/4/2017 2:21	60	29/4/2017 3:26	61	30/4/2017 4:31	61		
22/													

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
30/4/2017 23:46	57	2/5/2017 0:51	62	3/5/2017 1:56	62	4/5/2017 3:01	60	5/5/2017 4:06	58	6/5/2017 5:11	62
30/4/2017 23:51	57	2/5/2017 0:56	62	3/5/2017 2:01	63	4/5/2017 3:06	60	5/5/2017 4:11	59	6/5/2017 5:16	62
30/4/2017 23:56	50	2/5/2017 1:01	62	3/5/2017 2:06	63	4/5/2017 3:11	59	5/5/2017 4:16	59	6/5/2017 5:21	62
1/5/2017 0:01	58	2/5/2017 1:06	61	3/5/2017 2:11	62	4/5/2017 3:16	59	5/5/2017 4:21	61	6/5/2017 5:26	62
1/5/2017 0:06	48	2/5/2017 1:11	61	3/5/2017 2:16	62	4/5/2017 3:21	59	5/5/2017 4:26	60	6/5/2017 5:31	62
1/5/2017 0:11	54	2/5/2017 1:16	61	3/5/2017 2:21	62	4/5/2017 3:26	60	5/5/2017 4:31	61	6/5/2017 5:36	62
1/5/2017 0:16	63	2/5/2017 1:21	62	3/5/2017 2:26	62	4/5/2017 3:31	59	5/5/2017 4:36	60	6/5/2017 5:41	63
1/5/2017 0:21	48	2/5/2017 1:26	61	3/5/2017 2:31	61	4/5/2017 3:36	59	5/5/2017 4:41	60	6/5/2017 5:46	63
1/5/2017 0:26	47	2/5/2017 1:31	60	3/5/2017 2:36	62	4/5/2017 3:41	59	5/5/2017 4:46	58	6/5/2017 5:51	62
1/5/2017 0:31	48	2/5/2017 1:36	54	3/5/2017 2:41	61	4/5/2017 3:46	59	5/5/2017 4:51	60	6/5/2017 5:56	50
1/5/2017 0:36	63	2/5/2017 1:41	61	3/5/2017 2:46	62	4/5/2017 3:51	58	5/5/2017 4:56	59	6/5/2017 6:01	52
1/5/2017 0:41	63	2/5/2017 1:46	60	3/5/2017 2:51	68	4/5/2017 3:56	56	5/5/2017 5:01	60	6/5/2017 6:06	57
1/5/2017 0:46	62	2/5/2017 1:51	60	3/5/2017 2:56	62	4/5/2017 4:01	59	5/5/2017 5:06	60	6/5/2017 6:11	59
1/5/2017 0:51	58	2/5/2017 1:56	60	3/5/2017 3:01	61	4/5/2017 4:06	58	5/5/2017 5:11	59	6/5/2017 6:16	59
1/5/2017 0:56	62	2/5/2017 2:01	60	3/5/2017 3:06	62	4/5/2017 4:11	59	5/5/2017 5:16	60	6/5/2017 6:21	59
1/5/2017 1:01	63	2/5/2017 2:06	60	3/5/2017 3:11	61	4/5/2017 4:16	60	5/5/2017 5:21	61	6/5/2017 6:26	61
1/5/2017 1:06	63	2/5/2017 2:11	60	3/5/2017 3:16	60	4/5/2017 4:21	59	5/5/2017 5:26	61	6/5/2017 6:31	59
1/5/2017 1:11	62	2/5/2017 2:16	60	3/5/2017 3:21	62	4/5/2017 4:26	58	5/5/2017 5:31	61	6/5/2017 6:36	60
1/5/2017 1:16	62	2/5/2017 2:21	60	3/5/2017 3:26	60	4/5/2017 4:31	60	5/5/2017 5:36	62	6/5/2017 6:41	62
1/5/2017 1:21	63	2/5/2017 2:26	60	3/5/2017 3:31	60	4/5/2017 4:36	57	5/5/2017 5:41	62	6/5/2017 6:46	60
1/5/2017 1:26	62	2/5/2017 2:31	60	3/5/2017 3:36	60	4/5/2017 4:41	59	5/5/2017 5:46	62	6/5/2017 6:51	62
1/5/2017 1:31	62	2/5/2017 2:36	60	3/5/2017 3:41	61	4/5/2017 4:46	58	5/5/2017 5:51	62	6/5/2017 6:56	61
1/5/2017 1:36	62	2/5/2017 2:41	58	3/5/2017 3:46	60	4/5/2017 4:51	59	5/5/2017 5:56	53	6/5/2017 23:01	63
1/5/2017 1:41	52	2/5/2017 2:46	58	3/5/2017 3:51	61	4/5/2017 4:56	60	5/5/2017 6:01	62	6/5/2017 23:06	63
1/5/2017 1:46	62	2/5/2017 2:51	60	3/5/2017 3:56	60	4/5/2017 5:01	59	5/5/2017 6:06	58	6/5/2017 23:11	61
1/5/2017 1:51	62	2/5/2017 2:56	60	3/5/2017 4:01	60	4/5/2017 5:06	59	5/5/2017 6:11	53	6/5/2017 23:16	59
1/5/2017 1:56	62	2/5/2017 3:01	58	3/5/2017 4:06	60	4/5/2017 5:11	59	5/5/2017 6:16	59	6/5/2017 23:21	61
1/5/2017 2:01	62	2/5/2017 3:06	58	3/5/2017 4:11	60	4/5/2017 5:16	59	5/5/2017 6:21	59	6/5/2017 23:26	61
1/5/2017 2:06	62	2/5/2017 3:11	59	3/5/2017 4:16	60	4/5/2017 5:21	61	5/5/2017 6:26	60	6/5/2017 23:31	60
1/5/2017 2:11	61	2/5/2017 3:16	58	3/5/2017 4:21	60	4/5/2017 5:26	61	5/5/2017 6:31	62	6/5/2017 23:36	59
1/5/2017 2:16	59	2/5/2017 3:21	60	3/5/2017 4:26	60	4/5/2017 5:31	60	5/5/2017 6:36	61	6/5/2017 23:41	63
1/5/2017 2:21	60	2/5/2017 3:26	60	3/5/2017 4:31	61	4/5/2017 5:36	60	5/5/2017 6:41	62	6/5/2017 23:46	58
1/5/2017 2:26	62	2/5/2017 3:31	59	3/5/2017 4:36	60	4/5/2017 5:41	61	5/5/2017 6:46	63	6/5/2017 23:51	58
1/5/2017 2:31	62	2/5/2017 3:36	60	3/5/2017 4:41	60	4/5/2017 5:46	61	5/5/2017 6:51	63	6/5/2017 23:56	60
1/5/2017 2:36	62	2/5/2017 3:41	59	3/5/2017 4:46	59	4/5/2017 5:51	62	5/5/2017 6:56	64	7/5/2017 0:01	59
1/5/2017 2:41	60	2/5/2017 3:46	57	3/5/2017 4:51	62	4/5/2017 5:56	62	5/5/2017 23:01	59	7/5/2017 0:06	59
1/5/2017 2:46	61	2/5/2017 3:51	58	3/5/2017 4:56	61	4/5/2017 6:01	62	5/5/2017 23:06	60	7/5/2017 0:11	50
1/5/2017 2:51	60	2/5/2017 3:56	59	3/5/2017 5:01	61	4/5/2017 6:06	45	5/5/2017 23:11	61	7/5/2017 0:16	59
1/5/2017 2:56	61	2/5/2017 4:01	58	3/5/2017 5:06	61	4/5/2017 6:11	58	5/5/2017 23:16	62	7/5/2017 0:21	56
1/5/2017 3:01	61	2/5/2017 4:06	59	3/5/2017 5:11	60	4/5/2017 6:16	63	5/5/2017 23:21	60	7/5/2017 0:26	55
1/5/2017 3:06	61	2/5/2017 4:11	60	3/5/2017 5:16	61	4/5/2017 6:21	58	5/5/2017 23:26	60	7/5/2017 0:31	37
1/5/2017 3:11	61	2/5/2017 4:16	60	3/5/2017 5:21	61	4/5/2017 6:26	59	5/5/2017 23:31	59	7/5/2017 0:36	63
1/5/2017 3:16	60	2/5/2017 4:21	59	3/5/2017 5:26	61	4/5/2017 6:31	61	5/5/2017 23:36	59	7/5/2017 0:41	54
1/5/2017 3:21	61	2/5/2017 4:26	59	3/5/2017 5:31	61	4/5/2017 6:36	60	5/5/2017 23:41	58	7/5/2017 0:46	63
1/5/2017 3:26	59	2/5/2017 4:31	60	3/5/2017 5:36	62	4/5/2017 6:41	62	5/5/2017 23:46	60	7/5/2017 0:51	53
1/5/2017 3:31	60	2/5/2017 4:36	59	3/5/2017 5:41	62	4/5/2017 6:46	63	5/5/2017 23:51	61	7/5/2017 0:56	63
1/5/2017 3:36	59	2/5/2017 4:41	59	3/5/2017 5:46	59	4/5/2017 6:51	63	5/5/2017 23:56	59	7/5/2017 1:01	63
1/5/2017 3:41	60	2/5/2017 4:46	59	3/5/2017 5:51	62	4/5/2017 6:56	63	6/5/2017 0:01	62	7/5/2017 1:06	63
1/5/2017 3:46	59	2/5/2017 4:51	57	3/5/2017 5:56	61	4/5/2017 23:01	61	6/5/2017 0:06	59	7/5/2017 1:11	63
1/5/2017 3:51	61	2/5/2017 4:56	59	3/5/2017 6:01	45	4/5/2017 23:06	60	6/5/2017 0:11	60	7/5/2017 1:16	58
1/5/2017 3:56	61	2/5/2017 5:01	59	3/5/2017 6:06	62	4/5/2017 23:11	60	6/5/2017 0:16	58	7/5/2017 1:21	54
1/5/2017 4:01	60	2/5/2017 5:06	60	3/5/2017 6:11	62	4/5/2017 23:16	61	6/5/2017 0:21	57	7/5/2017 1:26	62
1/5/2017 4:06	60	2/5/2017 5:11	60	3/5/2017 6:16	63	4/5/2017 23:21	59	6/5/2017 0:26	60	7/5/2017 1:31	55
1/5/2017 4:11	60	2/5/2017 5:16	60	3/5/2017 6:21	63	4/5/2017 23:26	60	6/5/2017 0:31	59	7/5/2017 1:36	53
1/5/2017 4:16	59	2/5/2017 5:21	53	3/5/2017 6:26	63	4/5/2017 23:31	61	6/5/2017 0:36	55	7/5/2017 1:41	63
1/5/2017 4:21	59	2/5/2017 5:26	60	3/5/2017 6:31	51	4/5/2017 23:36	60	6/5/2017 0:41	50	7/5/2017 1:46	62
1/5/2017 4:26	59	2/5/2017 5:31	61	3/5/2017 6:36	50	4/5/2017 23:41	61	6/5/2017 0:46	59	7/5/2017 1:51	61
1/5/2017 4:31	61	2/5/2017 5:36	62	3/5/2017 6:41	61	4/5/2017 23:46	58	6/5/2017 0:51	49	7/5/2017 1:56	62
1/5/2017 4:36	60	2/5/2017 5:41	60	3/5/2017 6:46	56	4/5/2017 23:51	58	6/5/2017 0:56	54	7/5/2017 2:01	62
1/5/2017 4:41	50	2/5/2017 5:46	62	3/5/2017 6:51	63	4/5/2017 23:56	57	6/5/2017 1:01	55	7/5/2017 2:06	61
1/5/2017 4:46	60	2/5/2017 5:51	63	3/5/2017 6:56	54	5/5/2017 0:01	57	6/5/2017 1:06	55	7/5/2017 2:11	62
1/5/2017 4:51	61	2/5/2017 5:56	62	3/5/2017 23:01	57	5/5/2017 0:06	49	6/5/2017 1:11	54	7/5/2017 2:16	63
1/5/2017 4:56	60	2/5/2017 6:01	62	3/5/2017 23:06	57	5/5/2017 0:11	52	6/5/2017 1:16	55	7/5/2017 2:21	62
1/5/2017 5:01	60	2/5/2017 6:06	59	3/5/2017 23:11	60	5/5/2017 0:16	55	6/5/2017 1:21	63	7/5/2017 2:26	62
1/5/2017 5:06	61	2/5/2017 6:11	63	3/5/2017 23:16	56	5/5/2017 0:21	54	6/5/2017 1:26	63	7/5/2017 2:31	62
1/5/2017 5:11	61	2/5/2017 6:16	56	3/5/2017 23:21	59	5/5/2017 0:26	63	6/5/2017 1:31	63	7/5/2017 2:36	62
1/5/2017 5:16	60	2/5/2017 6:21	57	3/5/2017 23:26	58	5/5/2017 0:31	63	6/5/2017 1:36	63	7/5/2017 2:41	62
1/5/2017 5:21	61	2/5/2017 6:26	59	3/5/2017 23:31	58	5/5/2017 0:36	63	6/5/2017 1:41	58	7/5/2017 2:46	62
1/5/2017 5:26	61	2/5/2017 6:31	59	3/5/2017 23:36	59	5/5/2017 0:41	51	6/5/2017 1:46	63	7/5/2017 2:51	62
1/5/2017 5:31	60	2/5/2017 6:36	61	3/5/2017 23:41	57	5/5/2017 0:46	62	6/5/2017 1:51	63	7/5/2017 2:56	62
1/5/2017 5:36	60	2/5/2017 6:41	60	3/5/2017 23:46	58	5/5/2017 0:51	63	6/5/2017 1:56	63	7/5/2017 3:01	62
1/5/2017 5:41	61	2/5/2017 6:46	63	3/5/2017 23:51	58	5/5/2017 0:56	63	6/5/2017 2:01	46	7/5/2017 3:06	61
1/5/2017 5:46	61	2/5/2017 6:51	64	3/5/2017 23:56	52	5/5/2017 1:01	63	6/5/2017 2:06	51	7/5/2017 3:11	61
1/5/2017 5:51	62	2/5/2017 6:56	63	4/5/2017 0:01	63	5/5/2017 1:06	62	6/5/2017 2:11	62	7/5/2017 3:16	61
1/5/2017 5:56	62	2/5/2017 23:01	59	4/5/2017 0:06	63	5/5/2017 1:11	62	6/5/2017 2:16	43	7/5/2017 3:21	61
1/5/2017 6:01	50	2/5/2017 23:06	61	4/5/2017 0:11	51	5/5/2017 1:16	63	6/5/2017 2:21	63	7/5/2017 3:26	62
1/5/2017 6:06	62	2/5/2017 23:11	61	4/5/2017 0:16	49	5/5/2017 1:21	61	6/5/2017 2:26	63	7/5/2017 3:31	61
1/5/2017 6:11	63	2/5/2017 23:16	60	4/5/2017 0:21	63	5/5/2017 1:26	62	6/5/2017 2:31	50	7/5/2017 3:36	61
1/5/2017 6:16	48	2/5/2017 23:21	60	4/5/2017 0:26							

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)											
7/5/2017 6:16	53	8/5/2017 23:21	62	10/5/2017 0:26	63	11/5/2017 1:31	60	12/5/2017 2:36	60	13/5/2017 3:41	61		
7/5/2017 6:21	63	8/5/2017 23:26	61	10/5/2017 0:31	63	11/5/2017 1:36	60	12/5/2017 2:41	61	13/5/2017 3:46	61		
7/5/2017 6:26	63	8/5/2017 23:31	61	10/5/2017 0:36	56	11/5/2017 1:41	60	12/5/2017 2:46	60	13/5/2017 3:51	60		
7/5/2017 6:31	57	8/5/2017 23:36	60	10/5/2017 0:41	63	11/5/2017 1:46	61	12/5/2017 2:51	60	13/5/2017 3:56	60		
7/5/2017 6:36	60	8/5/2017 23:41	58	10/5/2017 0:46	62	11/5/2017 1:51	65	12/5/2017 2:56	60	13/5/2017 4:01	60		
7/5/2017 6:41	55	8/5/2017 23:46	60	10/5/2017 0:51	62	11/5/2017 1:56	60	12/5/2017 3:01	60	13/5/2017 4:06	61		
7/5/2017 6:46	63	8/5/2017 23:51	58	10/5/2017 0:56	62	11/5/2017 2:01	60	12/5/2017 3:06	61	13/5/2017 4:11	60		
7/5/2017 6:51	63	8/5/2017 23:56	59	10/5/2017 1:01	61	11/5/2017 2:06	59	12/5/2017 3:11	60	13/5/2017 4:16	60		
7/5/2017 6:56	58	9/5/2017 0:01	56	10/5/2017 1:06	62	11/5/2017 2:11	59	12/5/2017 3:16	55	13/5/2017 4:21	60		
7/5/2017 23:01	60	9/5/2017 0:06	58	10/5/2017 1:11	62	11/5/2017 2:16	59	12/5/2017 3:21	59	13/5/2017 4:26	60		
7/5/2017 23:06	58	9/5/2017 0:11	49	10/5/2017 1:16	61	11/5/2017 2:21	61	12/5/2017 3:26	63	13/5/2017 4:31	60		
7/5/2017 23:11	60	9/5/2017 0:16	54	10/5/2017 1:21	61	11/5/2017 2:26	61	12/5/2017 3:31	63	13/5/2017 4:36	61		
7/5/2017 23:16	57	9/5/2017 0:21	54	10/5/2017 1:26	62	11/5/2017 2:31	60	12/5/2017 3:36	62	13/5/2017 4:41	60		
7/5/2017 23:21	56	9/5/2017 0:26	51	10/5/2017 1:31	61	11/5/2017 2:36	62	12/5/2017 3:41	63	13/5/2017 4:46	60		
7/5/2017 23:26	54	9/5/2017 0:31	57	10/5/2017 1:36	62	11/5/2017 2:41	61	12/5/2017 3:46	60	13/5/2017 4:51	60		
7/5/2017 23:31	57	9/5/2017 0:36	63	10/5/2017 1:41	60	11/5/2017 2:46	60	12/5/2017 3:51	60	13/5/2017 4:56	61		
7/5/2017 23:36	54	9/5/2017 0:41	63	10/5/2017 1:46	62	11/5/2017 2:51	55	12/5/2017 3:56	59	13/5/2017 5:01	59		
7/5/2017 23:41	53	9/5/2017 0:46	62	10/5/2017 1:51	61	11/5/2017 2:56	60	12/5/2017 4:01	60	13/5/2017 5:06	61		
7/5/2017 23:46	53	9/5/2017 0:51	62	10/5/2017 1:56	62	11/5/2017 3:01	57	12/5/2017 4:06	60	13/5/2017 5:11	61		
7/5/2017 23:51	50	9/5/2017 0:56	63	10/5/2017 2:01	60	11/5/2017 3:06	63	12/5/2017 4:11	59	13/5/2017 5:16	62		
7/5/2017 23:56	58	9/5/2017 1:01	62	10/5/2017 2:06	61	11/5/2017 3:11	51	12/5/2017 4:16	59	13/5/2017 5:21	60		
8/5/2017 0:01	63	9/5/2017 1:06	62	10/5/2017 2:11	61	11/5/2017 3:16	59	12/5/2017 4:21	59	13/5/2017 5:26	61		
8/5/2017 0:06	63	9/5/2017 1:11	52	10/5/2017 2:16	61	11/5/2017 3:21	56	12/5/2017 4:26	60	13/5/2017 5:31	61		
8/5/2017 0:11	52	9/5/2017 1:16	56	10/5/2017 2:21	60	11/5/2017 3:26	55	12/5/2017 4:31	61	13/5/2017 5:36	61		
8/5/2017 0:16	58	9/5/2017 1:21	63	10/5/2017 2:26	59	11/5/2017 3:31	55	12/5/2017 4:36	60	13/5/2017 5:41	62		
8/5/2017 0:21	63	9/5/2017 1:26	63	10/5/2017 2:31	60	11/5/2017 3:36	61	12/5/2017 4:41	60	13/5/2017 5:46	62		
8/5/2017 0:26	62	9/5/2017 1:31	62	10/5/2017 2:36	59	11/5/2017 3:41	59	12/5/2017 4:46	58	13/5/2017 5:51	63		
8/5/2017 0:31	62	9/5/2017 1:36	63	10/5/2017 2:41	60	11/5/2017 3:46	60	12/5/2017 4:51	60	13/5/2017 5:56	62		
8/5/2017 0:36	62	9/5/2017 1:41	53	10/5/2017 2:46	59	11/5/2017 3:51	60	12/5/2017 4:56	60	13/5/2017 6:01	62		
8/5/2017 0:41	61	9/5/2017 1:46	63	10/5/2017 2:51	59	11/5/2017 3:56	60	12/5/2017 5:01	60	13/5/2017 6:06	62		
8/5/2017 0:46	62	9/5/2017 1:51	63	10/5/2017 2:56	60	11/5/2017 4:01	59	12/5/2017 5:06	60	13/5/2017 6:11	62		
8/5/2017 0:51	60	9/5/2017 1:56	63	10/5/2017 3:01	60	11/5/2017 4:06	59	12/5/2017 5:11	60	13/5/2017 6:16	59		
8/5/2017 0:56	62	9/5/2017 2:01	48	10/5/2017 3:06	60	11/5/2017 4:11	59	12/5/2017 5:16	60	13/5/2017 6:21	57		
8/5/2017 1:01	62	9/5/2017 2:06	63	10/5/2017 3:11	59	11/5/2017 4:16	59	12/5/2017 5:21	61	13/5/2017 6:26	58		
8/5/2017 1:06	62	9/5/2017 2:11	47	10/5/2017 3:16	63	11/5/2017 4:21	60	12/5/2017 5:26	62	13/5/2017 6:31	53		
8/5/2017 1:11	62	9/5/2017 2:16	63	10/5/2017 3:21	63	11/5/2017 4:26	59	12/5/2017 5:31	55	13/5/2017 6:36	54		
8/5/2017 1:16	62	9/5/2017 2:21	63	10/5/2017 3:26	62	11/5/2017 4:31	61	12/5/2017 5:36	63	13/5/2017 6:41	57		
8/5/2017 1:21	61	9/5/2017 2:26	63	10/5/2017 3:31	61	11/5/2017 4:36	61	12/5/2017 5:41	62	13/5/2017 6:46	61		
8/5/2017 1:26	61	9/5/2017 2:31	62	10/5/2017 3:36	59	11/5/2017 4:41	61	12/5/2017 5:46	62	13/5/2017 6:51	59		
8/5/2017 1:31	60	9/5/2017 2:36	63	10/5/2017 3:41	60	11/5/2017 4:46	60	12/5/2017 5:51	62	13/5/2017 6:56	61		
8/5/2017 1:36	60	9/5/2017 2:41	62	10/5/2017 3:46	60	11/5/2017 4:51	60	12/5/2017 5:56	63	13/5/2017 23:01	61		
8/5/2017 1:41	60	9/5/2017 2:46	63	10/5/2017 3:51	59	11/5/2017 4:56	61	12/5/2017 6:01	62	13/5/2017 23:06	61		
8/5/2017 1:46	62	9/5/2017 2:51	62	10/5/2017 3:56	60	11/5/2017 5:01	60	12/5/2017 6:06	63	13/5/2017 23:11	60		
8/5/2017 1:51	59	9/5/2017 2:56	63	10/5/2017 4:01	60	11/5/2017 5:06	60	12/5/2017 6:11	53	13/5/2017 23:16	61		
8/5/2017 1:56	61	9/5/2017 3:01	62	10/5/2017 4:06	60	11/5/2017 5:11	61	12/5/2017 6:16	58	13/5/2017 23:21	61		
8/5/2017 2:01	61	9/5/2017 3:06	61	10/5/2017 4:11	59	11/5/2017 5:16	61	12/5/2017 6:21	54	13/5/2017 23:26	60		
8/5/2017 2:06	61	9/5/2017 3:11	61	10/5/2017 4:16	60	11/5/2017 5:21	61	12/5/2017 6:26	61	13/5/2017 23:31	61		
8/5/2017 2:11	60	9/5/2017 3:16	62	10/5/2017 4:21	60	11/5/2017 5:26	61	12/5/2017 6:31	62	13/5/2017 23:36	61		
8/5/2017 2:16	61	9/5/2017 3:21	62	10/5/2017 4:26	60	11/5/2017 5:31	61	12/5/2017 6:36	61	13/5/2017 23:41	61		
8/5/2017 2:21	61	9/5/2017 3:26	61	10/5/2017 4:31	61	11/5/2017 5:36	61	12/5/2017 6:41	61	13/5/2017 23:46	61		
8/5/2017 2:26	60	9/5/2017 3:31	62	10/5/2017 4:36	61	11/5/2017 5:41	61	12/5/2017 6:46	63	13/5/2017 23:51	59		
8/5/2017 2:31	59	9/5/2017 3:36	62	10/5/2017 4:41	61	11/5/2017 5:46	62	12/5/2017 6:51	64	13/5/2017 23:56	56		
8/5/2017 2:36	60	9/5/2017 3:41	61	10/5/2017 4:46	60	11/5/2017 5:51	62	12/5/2017 6:56	62	14/5/2017 0:01	60		
8/5/2017 2:41	59	9/5/2017 3:46	61	10/5/2017 4:51	61	11/5/2017 5:56	63	12/5/2017 23:01	61	14/5/2017 0:06	60		
8/5/2017 2:46	59	9/5/2017 3:51	60	10/5/2017 4:56	60	11/5/2017 6:01	62	12/5/2017 23:06	57	14/5/2017 0:11	60		
8/5/2017 2:51	59	9/5/2017 3:56	60	10/5/2017 5:01	60	11/5/2017 6:06	54	12/5/2017 23:11	58	14/5/2017 0:16	57		
8/5/2017 2:56	60	9/5/2017 4:01	60	10/5/2017 5:06	60	11/5/2017 6:11	57	12/5/2017 23:16	58	14/5/2017 0:21	60		
8/5/2017 3:01	59	9/5/2017 4:06	60	10/5/2017 5:11	61	11/5/2017 6:16	63	12/5/2017 23:21	58	14/5/2017 0:26	58		
8/5/2017 3:06	58	9/5/2017 4:11	61	10/5/2017 5:16	54	11/5/2017 6:21	58	12/5/2017 23:26	60	14/5/2017 0:31	62		
8/5/2017 3:11	59	9/5/2017 4:16	60	10/5/2017 5:21	56	11/5/2017 6:26	58	12/5/2017 23:31	57	14/5/2017 0:36	58		
8/5/2017 3:16	59	9/5/2017 4:21	60	10/5/2017 5:26	63	11/5/2017 6:31	62	12/5/2017 23:36	58	14/5/2017 0:41	54		
8/5/2017 3:21	61	9/5/2017 4:26	60	10/5/2017 5:31	62	11/5/2017 6:36	61	12/5/2017 23:41	57	14/5/2017 0:46	56		
8/5/2017 3:26	61	9/5/2017 4:31	59	10/5/2017 5:36	63	11/5/2017 6:41	63	12/5/2017 23:46	55	14/5/2017 0:51	51		
8/5/2017 3:31	58	9/5/2017 4:36	61	10/5/2017 5:41	50	11/5/2017 6:46	63	12/5/2017 23:51	57	14/5/2017 0:56	51		
8/5/2017 3:36	59	9/5/2017 4:41	61	10/5/2017 5:46	63	11/5/2017 6:51	63	12/5/2017 23:56	55	14/5/2017 1:01	54		
8/5/2017 3:41	59	9/5/2017 4:46	61	10/5/2017 5:51	61	11/5/2017 6:56	64	13/5/2017 0:01	56	14/5/2017 1:06	63		
8/5/2017 3:46	58	9/5/2017 4:51	60	10/5/2017 5:56	51	11/5/2017 23:01	61	13/5/2017 0:06	54	14/5/2017 1:11	63		
8/5/2017 3:51	60	9/5/2017 4:56	61	10/5/2017 6:01	60	11/5/2017 23:06	61	13/5/2017 0:11	57	14/5/2017 1:16	63		
8/5/2017 3:56	59	9/5/2017 5:01	59	10/5/2017 6:06	59	11/5/2017 23:11	60	13/5/2017 0:16	55	14/5/2017 1:21	54		
8/5/2017 4:01	60	9/5/2017 5:06	61	10/5/2017 6:11	58	11/5/2017 23:16	60	13/5/2017 0:21	58	14/5/2017 1:26	57		
8/5/2017 4:06	59	9/5/2017 5:11	62	10/5/2017 6:16	63	11/5/2017 23:21	56	13/5/2017 0:26	58	14/5/2017 1:31	63		
8/5/2017 4:11	59	9/5/2017 5:16	63	10/5/2017 6:21	63	11/5/2017 23:26	59	13/5/2017 0:31	54	14/5/2017 1:36	63		
8/5/2017 4:16	60	9/5/2017 5:21	63	10/5/2017 6:26	63	11/5/2017 23:31	61						

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)									
14/5/2017 4:46	60	15/5/2017 5:51	61	16/5/2017 6:56	64	18/5/2017 0:01	56	19/5/2017 1:06	62	20/5/2017 2:11	63
14/5/2017 4:51	60	15/5/2017 5:56	63	16/5/2017 23:01	62	18/5/2017 0:06	58	19/5/2017 1:11	57	20/5/2017 2:16	62
14/5/2017 4:56	61	15/5/2017 6:01	63	16/5/2017 23:06	59	18/5/2017 0:11	54	19/5/2017 1:16	62	20/5/2017 2:21	62
14/5/2017 5:01	61	15/5/2017 6:06	53	16/5/2017 23:11	59	18/5/2017 0:16	55	19/5/2017 1:21	62	20/5/2017 2:26	62
14/5/2017 5:06	60	15/5/2017 6:11	48	16/5/2017 23:16	59	18/5/2017 0:21	56	19/5/2017 1:26	63	20/5/2017 2:31	62
14/5/2017 5:11	60	15/5/2017 6:16	60	16/5/2017 23:21	60	18/5/2017 0:26	56	19/5/2017 1:31	62	20/5/2017 2:36	62
14/5/2017 5:16	61	15/5/2017 6:21	58	16/5/2017 23:26	61	18/5/2017 0:31	55	19/5/2017 1:36	62	20/5/2017 2:41	62
14/5/2017 5:21	61	15/5/2017 6:26	60	16/5/2017 23:31	58	18/5/2017 0:36	63	19/5/2017 1:41	58	20/5/2017 2:46	62
14/5/2017 5:26	62	15/5/2017 6:31	59	16/5/2017 23:36	59	18/5/2017 0:41	51	19/5/2017 1:46	61	20/5/2017 2:51	62
14/5/2017 5:31	63	15/5/2017 6:36	60	16/5/2017 23:41	58	18/5/2017 0:46	56	19/5/2017 1:51	62	20/5/2017 2:56	62
14/5/2017 5:36	62	15/5/2017 6:41	62	16/5/2017 23:46	52	18/5/2017 0:51	48	19/5/2017 1:56	62	20/5/2017 3:01	62
14/5/2017 5:41	61	15/5/2017 6:46	62	16/5/2017 23:51	53	18/5/2017 0:56	63	19/5/2017 2:01	61	20/5/2017 3:06	61
14/5/2017 5:46	62	15/5/2017 6:51	63	16/5/2017 23:56	56	18/5/2017 1:01	63	19/5/2017 2:06	61	20/5/2017 3:11	61
14/5/2017 5:51	62	15/5/2017 6:56	63	17/5/2017 0:01	57	18/5/2017 1:06	62	19/5/2017 2:11	61	20/5/2017 3:16	61
14/5/2017 5:56	63	15/5/2017 23:01	60	17/5/2017 0:06	51	18/5/2017 1:11	50	19/5/2017 2:16	61	20/5/2017 3:21	60
14/5/2017 6:01	44	15/5/2017 23:06	60	17/5/2017 0:11	63	18/5/2017 1:16	62	19/5/2017 2:21	61	20/5/2017 3:26	61
14/5/2017 6:06	62	15/5/2017 23:11	58	17/5/2017 0:16	54	18/5/2017 1:21	62	19/5/2017 2:26	62	20/5/2017 3:31	61
14/5/2017 6:11	52	15/5/2017 23:16	57	17/5/2017 0:21	57	18/5/2017 1:26	61	19/5/2017 2:31	61	20/5/2017 3:36	60
14/5/2017 6:16	63	15/5/2017 23:21	58	17/5/2017 0:26	57	18/5/2017 1:31	61	19/5/2017 2:36	61	20/5/2017 3:41	61
14/5/2017 6:21	58	15/5/2017 23:26	62	17/5/2017 0:31	57	18/5/2017 1:36	62	19/5/2017 2:41	61	20/5/2017 3:46	61
14/5/2017 6:26	60	15/5/2017 23:31	60	17/5/2017 0:36	50	18/5/2017 1:41	62	19/5/2017 2:46	59	20/5/2017 3:51	62
14/5/2017 6:31	53	15/5/2017 23:36	58	17/5/2017 0:41	63	18/5/2017 1:46	61	19/5/2017 2:51	60	20/5/2017 3:56	60
14/5/2017 6:36	63	15/5/2017 23:41	53	17/5/2017 0:46	63	18/5/2017 1:51	62	19/5/2017 2:56	61	20/5/2017 4:01	61
14/5/2017 6:41	56	15/5/2017 23:46	55	17/5/2017 0:51	49	18/5/2017 1:56	60	19/5/2017 3:01	60	20/5/2017 4:06	60
14/5/2017 6:46	61	15/5/2017 23:51	55	17/5/2017 0:56	47	18/5/2017 2:01	61	19/5/2017 3:06	60	20/5/2017 4:11	61
14/5/2017 6:51	55	15/5/2017 23:56	57	17/5/2017 1:01	62	18/5/2017 2:06	62	19/5/2017 3:11	60	20/5/2017 4:16	61
14/5/2017 6:56	56	16/5/2017 0:01	53	17/5/2017 1:06	63	18/5/2017 2:11	61	19/5/2017 3:16	60	20/5/2017 4:21	61
14/5/2017 23:01	63	16/5/2017 0:06	48	17/5/2017 1:11	62	18/5/2017 2:16	61	19/5/2017 3:21	60	20/5/2017 4:26	62
14/5/2017 23:06	59	16/5/2017 0:11	52	17/5/2017 1:16	62	18/5/2017 2:21	61	19/5/2017 3:26	60	20/5/2017 4:31	60
14/5/2017 23:11	59	16/5/2017 0:16	50	17/5/2017 1:21	65	18/5/2017 2:26	61	19/5/2017 3:31	61	20/5/2017 4:36	60
14/5/2017 23:16	58	16/5/2017 0:21	46	17/5/2017 1:26	62	18/5/2017 2:31	60	19/5/2017 3:36	60	20/5/2017 4:41	60
14/5/2017 23:21	59	16/5/2017 0:26	63	17/5/2017 1:31	62	18/5/2017 2:36	60	19/5/2017 3:41	60	20/5/2017 4:46	61
14/5/2017 23:26	56	16/5/2017 0:31	63	17/5/2017 1:36	63	18/5/2017 2:41	60	19/5/2017 3:46	60	20/5/2017 4:51	61
14/5/2017 23:31	50	16/5/2017 0:36	62	17/5/2017 1:41	62	18/5/2017 2:46	60	19/5/2017 3:51	59	20/5/2017 4:56	60
14/5/2017 23:36	55	16/5/2017 0:41	62	17/5/2017 1:46	61	18/5/2017 2:51	61	19/5/2017 3:56	59	20/5/2017 5:01	61
14/5/2017 23:41	54	16/5/2017 0:46	62	17/5/2017 1:51	62	18/5/2017 2:56	60	19/5/2017 4:01	59	20/5/2017 5:06	61
14/5/2017 23:46	56	16/5/2017 0:51	63	17/5/2017 1:56	62	18/5/2017 3:01	60	19/5/2017 4:06	60	20/5/2017 5:11	61
14/5/2017 23:51	63	16/5/2017 0:56	58	17/5/2017 2:01	62	18/5/2017 3:06	60	19/5/2017 4:11	59	20/5/2017 5:16	61
14/5/2017 23:56	55	16/5/2017 1:01	57	17/5/2017 2:06	61	18/5/2017 3:11	59	19/5/2017 4:16	59	20/5/2017 5:21	60
15/5/2017 0:01	63	16/5/2017 1:06	58	17/5/2017 2:11	61	18/5/2017 3:16	61	19/5/2017 4:21	60	20/5/2017 5:26	62
15/5/2017 0:06	63	16/5/2017 1:11	58	17/5/2017 2:16	61	18/5/2017 3:21	58	19/5/2017 4:26	61	20/5/2017 5:31	62
15/5/2017 0:11	62	16/5/2017 1:16	60	17/5/2017 2:21	61	18/5/2017 3:26	59	19/5/2017 4:31	59	20/5/2017 5:36	63
15/5/2017 0:16	63	16/5/2017 1:21	53	17/5/2017 2:26	62	18/5/2017 3:31	60	19/5/2017 4:36	60	20/5/2017 5:41	63
15/5/2017 0:21	63	16/5/2017 1:26	63	17/5/2017 2:31	60	18/5/2017 3:36	59	19/5/2017 4:41	60	20/5/2017 5:46	62
15/5/2017 0:26	62	16/5/2017 1:31	58	17/5/2017 2:36	59	18/5/2017 3:41	62	19/5/2017 4:46	59	20/5/2017 5:51	62
15/5/2017 0:31	63	16/5/2017 1:36	59	17/5/2017 2:41	60	18/5/2017 3:46	58	19/5/2017 4:51	59	20/5/2017 5:56	48
15/5/2017 0:36	61	16/5/2017 1:41	52	17/5/2017 2:46	60	18/5/2017 3:51	59	19/5/2017 4:56	60	20/5/2017 6:01	62
15/5/2017 0:41	61	16/5/2017 1:46	62	17/5/2017 2:51	60	18/5/2017 3:56	60	19/5/2017 5:01	61	20/5/2017 6:06	62
15/5/2017 0:46	62	16/5/2017 1:51	61	17/5/2017 2:56	61	18/5/2017 4:01	59	19/5/2017 5:06	61	20/5/2017 6:11	46
15/5/2017 0:51	62	16/5/2017 1:56	61	17/5/2017 3:01	60	18/5/2017 4:06	60	19/5/2017 5:11	61	20/5/2017 6:16	63
15/5/2017 0:56	62	16/5/2017 2:01	61	17/5/2017 3:06	60	18/5/2017 4:11	61	19/5/2017 5:16	59	20/5/2017 6:21	55
15/5/2017 1:01	61	16/5/2017 2:06	62	17/5/2017 3:11	60	18/5/2017 4:16	59	19/5/2017 5:21	61	20/5/2017 6:26	56
15/5/2017 1:06	61	16/5/2017 2:11	61	17/5/2017 3:16	58	18/5/2017 4:21	59	19/5/2017 5:26	61	20/5/2017 6:31	61
15/5/2017 1:11	60	16/5/2017 2:16	60	17/5/2017 3:21	60	18/5/2017 4:26	60	19/5/2017 5:31	62	20/5/2017 6:36	56
15/5/2017 1:16	62	16/5/2017 2:21	61	17/5/2017 3:26	58	18/5/2017 4:31	59	19/5/2017 5:36	62	20/5/2017 6:41	59
15/5/2017 1:21	67	16/5/2017 2:26	61	17/5/2017 3:31	59	18/5/2017 4:36	59	19/5/2017 5:41	61	20/5/2017 6:46	58
15/5/2017 1:26	61	16/5/2017 2:31	60	17/5/2017 3:36	60	18/5/2017 4:41	60	19/5/2017 5:46	62	20/5/2017 6:51	61
15/5/2017 1:31	61	16/5/2017 2:36	60	17/5/2017 3:41	59	18/5/2017 4:46	60	19/5/2017 5:51	61	20/5/2017 6:56	61
15/5/2017 1:36	60	16/5/2017 2:41	59	17/5/2017 3:46	59	18/5/2017 4:51	61	19/5/2017 5:56	63	20/5/2017 23:01	60
15/5/2017 1:41	59	16/5/2017 2:46	60	17/5/2017 3:51	60	18/5/2017 4:56	60	19/5/2017 6:01	40	20/5/2017 23:06	60
15/5/2017 1:46	59	16/5/2017 2:51	59	17/5/2017 3:56	59	18/5/2017 5:01	61	19/5/2017 6:06	45	20/5/2017 23:11	59
15/5/2017 1:51	61	16/5/2017 2:56	59	17/5/2017 4:01	58	18/5/2017 5:06	61	19/5/2017 6:11	52	20/5/2017 23:16	60
15/5/2017 1:56	60	16/5/2017 3:01	59	17/5/2017 4:06	59	18/5/2017 5:11	61	19/5/2017 6:16	56	20/5/2017 23:21	60
15/5/2017 2:01	61	16/5/2017 3:06	59	17/5/2017 4:11	58	18/5/2017 5:16	59	19/5/2017 6:21	59	20/5/2017 23:26	59
15/5/2017 2:06	60	16/5/2017 3:11	59	17/5/2017 4:16	60	18/5/2017 5:21	59	19/5/2017 6:26	60	20/5/2017 23:31	59
15/5/2017 2:11	59	16/5/2017 3:16	59	17/5/2017 4:21	60	18/5/2017 5:26	61	19/5/2017 6:31	61	20/5/2017 23:36	58
15/5/2017 2:16	59	16/5/2017 3:21	60	17/5/2017 4:26	60	18/5/2017 5:31	61	19/5/2017 6:36	60	20/5/2017 23:41	58
15/5/2017 2:21	60	16/5/2017 3:26	58	17/5/2017 4:31	60	18/5/2017 5:36	62	19/5/2017 6:41	63	20/5/2017 23:46	58
15/5/2017 2:26	60	16/5/2017 3:31	58	17/5/2017 4:36	60	18/5/2017 5:41	62	19/5/2017 6:46	63	20/5/2017 23:51	58
15/5/2017 2:31	60	16/5/2017 3:36	60	17/5/2017 4:41	60	18/5/2017 5:46	62	19/5/2017 6:51	64	20/5/2017 23:56	58
15/5/2017 2:36	59	16/5/2017 3:41	59	17/5/2017 4:46	59	18/5/2017 5:51	62	19/5/2017 6:56	63	21/5/2017 0:01	57
15/5/2017 2:41	59	16/5/2017 3:46	59	17/5/2017 4:51	62	18/5/2017 5:56	62	19/5/2017 23:01	62	21/5/2017 0:06	58
15/5/2017 2:46	58	16/5/2017 3:51	59	17/5/2017 4:56	61	18/5/2017 6:01	62	19/5/2017 23:06	62	21/5/2017 0:11	57
15/5/2017 2:51	58	16/5/2017 3:56	61	17/5/2017 5:01	61	18/5/2017 6:06	54	19/5/2017 23:11	63	21/5/2017 0:16	57
15/5/2017 2:56	58	16/5/2017 4:01	59	17/5/2017 5:06	59	18/5/2017 6:11	54	19/5/2017 23:16	61	21/5/2017 0:21	57
15/5/2017 3:01	60	16/5/2017 4:06	59	17/5/2017 5:11	60	18/5/2017 6:					

Real-time Noise Data		RTN3 (Po Leung Kuk Yu Lee Mo Fan Memorial School)					
21/5/2017 3:16	61	22/5/2017 4:21	60	23/5/2017 5:26	61	24/5/2017 6:31	68
21/5/2017 3:21	61	22/5/2017 4:26	58	23/5/2017 5:31	63	24/5/2017 6:36	69
21/5/2017 3:26	61	22/5/2017 4:31	60	23/5/2017 5:36	54	24/5/2017 6:41	69
21/5/2017 3:31	61	22/5/2017 4:36	59	23/5/2017 5:41	62	24/5/2017 6:46	68
21/5/2017 3:36	62	22/5/2017 4:41	60	23/5/2017 5:46	62	24/5/2017 6:51	67
21/5/2017 3:41	61	22/5/2017 4:46	58	23/5/2017 5:51	63	24/5/2017 6:56	66
21/5/2017 3:46	60	22/5/2017 4:51	60	23/5/2017 5:56	77	24/5/2017 23:01	60
21/5/2017 3:51	61	22/5/2017 4:56	61	23/5/2017 6:01	77	24/5/2017 23:06	60
21/5/2017 3:56	61	22/5/2017 5:01	60	23/5/2017 6:06	63	24/5/2017 23:11	60
21/5/2017 4:01	60	22/5/2017 5:06	60	23/5/2017 6:11	40	24/5/2017 23:16	61
21/5/2017 4:06	60	22/5/2017 5:11	60	23/5/2017 6:16	55	24/5/2017 23:21	62
21/5/2017 4:11	61	22/5/2017 5:16	59	23/5/2017 6:21	57	24/5/2017 23:26	61
21/5/2017 4:16	61	22/5/2017 5:21	61	23/5/2017 6:26	62	24/5/2017 23:31	60
21/5/2017 4:21	60	22/5/2017 5:26	60	23/5/2017 6:31	62	24/5/2017 23:36	62
21/5/2017 4:26	61	22/5/2017 5:31	61	23/5/2017 6:36	61	24/5/2017 23:41	57
21/5/2017 4:31	60	22/5/2017 5:36	62	23/5/2017 6:41	61	24/5/2017 23:46	58
21/5/2017 4:36	61	22/5/2017 5:41	62	23/5/2017 6:46	63	24/5/2017 23:51	61
21/5/2017 4:41	61	22/5/2017 5:46	63	23/5/2017 6:51	64	24/5/2017 23:56	57
21/5/2017 4:46	60	22/5/2017 5:51	54	23/5/2017 6:56	63	25/5/2017 0:01	60
21/5/2017 4:51	61	22/5/2017 5:56	63	23/5/2017 23:01	61	25/5/2017 0:06	56
21/5/2017 4:56	60	22/5/2017 6:01	62	23/5/2017 23:06	62	25/5/2017 0:11	60
21/5/2017 5:01	60	22/5/2017 6:06	63	23/5/2017 23:11	61	25/5/2017 0:16	56
21/5/2017 5:06	62	22/5/2017 6:11	51	23/5/2017 23:16	62	25/5/2017 0:21	57
21/5/2017 5:11	60	22/5/2017 6:16	62	23/5/2017 23:21	63	25/5/2017 0:26	54
21/5/2017 5:16	60	22/5/2017 6:21	58	23/5/2017 23:26	61	25/5/2017 0:31	63
21/5/2017 5:21	60	22/5/2017 6:26	60	23/5/2017 23:31	57	25/5/2017 0:36	56
21/5/2017 5:26	61	22/5/2017 6:31	61	23/5/2017 23:36	60	25/5/2017 0:41	63
21/5/2017 5:31	62	22/5/2017 6:36	61	23/5/2017 23:41	60	25/5/2017 0:46	40
21/5/2017 5:36	62	22/5/2017 6:41	62	23/5/2017 23:46	58	25/5/2017 0:51	57
21/5/2017 5:41	62	22/5/2017 6:46	63	23/5/2017 23:51	57	25/5/2017 0:56	63
21/5/2017 5:46	62	22/5/2017 6:51	63	23/5/2017 23:56	57	25/5/2017 1:01	62
21/5/2017 5:51	62	22/5/2017 6:56	63	24/5/2017 0:01	57	25/5/2017 1:06	62
21/5/2017 5:56	62	22/5/2017 23:01	64	24/5/2017 0:06	57	25/5/2017 1:11	63
21/5/2017 6:01	62	22/5/2017 23:06	64	24/5/2017 0:11	55	25/5/2017 1:16	62
21/5/2017 6:06	62	22/5/2017 23:11	63	24/5/2017 0:16	57	25/5/2017 1:21	62
21/5/2017 6:11	63	22/5/2017 23:16	63	24/5/2017 0:21	56	25/5/2017 1:26	62
21/5/2017 6:16	63	22/5/2017 23:21	63	24/5/2017 0:26	58	25/5/2017 1:31	62
21/5/2017 6:21	57	22/5/2017 23:26	61	24/5/2017 0:31	57	25/5/2017 1:36	61
21/5/2017 6:26	51	22/5/2017 23:31	61	24/5/2017 0:36	63	25/5/2017 1:41	62
21/5/2017 6:31	61	22/5/2017 23:36	60	24/5/2017 0:41	58	25/5/2017 1:46	61
21/5/2017 6:36	51	22/5/2017 23:41	58	24/5/2017 0:46	62	25/5/2017 1:51	61
21/5/2017 6:41	58	22/5/2017 23:46	59	24/5/2017 0:51	40	25/5/2017 1:56	62
21/5/2017 6:46	60	22/5/2017 23:51	56	24/5/2017 0:56	63	25/5/2017 2:01	62
21/5/2017 6:51	59	22/5/2017 23:56	57	24/5/2017 1:01	55	25/5/2017 2:06	61
21/5/2017 6:56	57	23/5/2017 0:01	57	24/5/2017 1:06	63	25/5/2017 2:11	63
21/5/2017 23:01	56	23/5/2017 0:06	57	24/5/2017 1:11	62	25/5/2017 2:16	60
21/5/2017 23:06	60	23/5/2017 0:11	46	24/5/2017 1:16	60	25/5/2017 2:21	65
21/5/2017 23:11	61	23/5/2017 0:16	58	24/5/2017 1:21	62	25/5/2017 2:26	67
21/5/2017 23:16	58	23/5/2017 0:21	59	24/5/2017 1:26	62	25/5/2017 2:31	61
21/5/2017 23:21	57	23/5/2017 0:26	56	24/5/2017 1:31	62	25/5/2017 2:36	61
21/5/2017 23:26	59	23/5/2017 0:31	61	24/5/2017 1:36	44	25/5/2017 2:41	61
21/5/2017 23:31	55	23/5/2017 0:36	57	24/5/2017 1:41	61	25/5/2017 2:46	60
21/5/2017 23:36	57	23/5/2017 0:41	54	24/5/2017 1:46	62	25/5/2017 2:51	61
21/5/2017 23:41	55	23/5/2017 0:46	63	24/5/2017 1:51	63	25/5/2017 2:56	59
21/5/2017 23:46	57	23/5/2017 0:51	63	24/5/2017 1:56	61	25/5/2017 3:01	61
21/5/2017 23:51	63	23/5/2017 0:56	63	24/5/2017 2:01	61	25/5/2017 3:06	60
21/5/2017 23:56	43	23/5/2017 1:01	62	24/5/2017 2:06	61	25/5/2017 3:11	60
22/5/2017 0:01	63	23/5/2017 1:06	62	24/5/2017 2:11	60	25/5/2017 3:16	59
22/5/2017 0:06	51	23/5/2017 1:11	62	24/5/2017 2:16	60	25/5/2017 3:21	60
22/5/2017 0:11	63	23/5/2017 1:16	61	24/5/2017 2:21	61	25/5/2017 3:26	59
22/5/2017 0:16	52	23/5/2017 1:21	61	24/5/2017 2:26	60	25/5/2017 3:31	61
22/5/2017 0:21	50	23/5/2017 1:26	62	24/5/2017 2:31	60	25/5/2017 3:36	60
22/5/2017 0:26	52	23/5/2017 1:31	61	24/5/2017 2:36	60	25/5/2017 3:41	60
22/5/2017 0:31	50	23/5/2017 1:36	61	24/5/2017 2:41	61	25/5/2017 3:46	59
22/5/2017 0:36	62	23/5/2017 1:41	63	24/5/2017 2:46	59	25/5/2017 3:51	60
22/5/2017 0:41	63	23/5/2017 1:46	62	24/5/2017 2:51	59	25/5/2017 3:56	60
22/5/2017 0:46	63	23/5/2017 1:51	62	24/5/2017 2:56	61	25/5/2017 4:01	60
22/5/2017 0:51	62	23/5/2017 1:56	61	24/5/2017 3:01	60	25/5/2017 4:06	59
22/5/2017 0:56	61	23/5/2017 2:01	62	24/5/2017 3:06	62	25/5/2017 4:11	61
22/5/2017 1:01	62	23/5/2017 2:06	61	24/5/2017 3:11	59	25/5/2017 4:16	59
22/5/2017 1:06	62	23/5/2017 2:11	61	24/5/2017 3:16	60	25/5/2017 4:21	60
22/5/2017 1:11	62	23/5/2017 2:16	61	24/5/2017 3:21	59	25/5/2017 4:26	59
22/5/2017 1:16	62	23/5/2017 2:21	61	24/5/2017 3:26	59	25/5/2017 4:31	60
22/5/2017 1:21	61	23/5/2017 2:26	61	24/5/2017 3:31	60	25/5/2017 4:36	59
22/5/2017 1:26	62	23/5/2017 2:31	60	24/5/2017 3:36	60	25/5/2017 4:41	60
22/5/2017 1:31	62	23/5/2017 2:36	61	24/5/2017 3:41	60	25/5/2017 4:46	60
22/5/2017 1:36	61	23/5/2017 2:41	62	24/5/2017 3:46	59	25/5/2017 4:51	59
22/5/2017 1:41	60	23/5/2017 2:46	61	24/5/2017 3:51	58	25/5/2017 4:56	61
22/5/2017 1:46	60	23/5/2017 2:51	61	24/5/2017 3:56	59	25/5/2017 5:01	60
22/5/2017 1:51	60	23/5/2017 2:56	61	24/5/2017 4:01	58	25/5/2017 5:06	61
22/5/2017 1:56	61	23/5/2017 3:01	61	24/5/2017 4:06	59	25/5/2017 5:11	60
22/5/2017 2:01	60	23/5/2017 3:06	60	24/5/2017 4:11	59	25/5/2017 5:16	61
22/5/2017 2:06	60	23/5/2017 3:11	61	24/5/2017 4:16	59	25/5/2017 5:21	61
22/5/2017 2:11	60	23/5/2017 3:16	61	24/5/2017 4:21	60	25/5/2017 5:26	62
22/5/2017 2:16	59	23/5/2017 3:21	60	24/5/2017 4:26	60	25/5/2017 5:31	62
22/5/2017 2:21	59	23/5/2017 3:26	61	24/5/2017 4:31	61	25/5/2017 5:36	62
22/5/2017 2:26	59	23/5/2017 3:31	60	24/5/2017 4:36	60	25/5/2017 5:41	61
22/5/2017 2:31	60	23/5/2017 3:36	61	24/5/2017 4:41	59	25/5/2017 5:46	62
22/5/2017 2:36	60	23/5/2017 3:41	60	24/5/2017 4:46	59	25/5/2017 5:51	62
22/5/2017 2:41	59	23/5/2017 3:46	59	24/5/2017 4:51	59	25/5/2017 5:56	63
22/5/2017 2:46	59	23/5/2017 3:51	59	24/5/2017 4:56	60	25/5/2017 6:01	51
22/5/2017 2:51	59	23/5/2017 3:56	59	24/5/2017 5:01	60	25/5/2017 6:06	63
22/5/2017 2:56	58	23/5/2017 4:01	59	24/5/2017 5:06	60	25/5/2017 6:11	56
22/5/2017 3:01	58	23/5/2017 4:06	59	24/5/2017 5:11	59	25/5/2017 6:16	59
22/5/2017 3:06	59	23/5/2017 4:11	60	24/5/2017 5:16	60	25/5/2017 6:21	60
22/5/2017 3:11	59	23/5/2017 4:16	59	24/5/2017 5:21	60	25/5/2017 6:26	60
22/5/2017 3:16	58	23/5/2017 4:21	61	24/5/2017 5:26	63	25/5/2017 6:31	61
22/5/2017 3:21	58	23/5/2017 4:26	60	24/5/2017 5:31	61	25/5/2017 6:36	62
22/5/2017 3:26	59	23/5/2017 4:31	61	24/5/2017 5:36	61	25/5/2017 6:41	63
22/5/2017 3:31	58	23/5/2017 4:36	59	24/5/2017 5:41	61	25/5/2017 6:46	63
22/5/2017 3:36	59	23/5/2017 4:41	60	24/5/2017 5:46	62	25/5/2017 6:51	63
22/5/2017 3:41	60	23/5/2017 4:46	60	24/5/2017 5:51	55	25/5/2017 6:56	63
22/5/2017 3:46	58	23/5/2017 4:51	61	24/5/2017 5:56	63	25/5/2017 23:01	60
22/5/2017 3:51	57	23/5/2017 4:56	61	24/5/2017 6:01	64	25/5/2017 23:06	61
22/5/2017 3:56	58	23/5/2017 5:01	59	24/5/2017 6:06	66	25/5/2017 23:11	60
22/5/2017 4:01	58	23/5/2017 5:06	60	24/5/2017 6:11	65	25/5/2017 23:16	60
22/5/2017 4:06	58	23/5/2017 5:11	60	24/5/2017 6:16	64	25/5/2017 23:21	61
22/5/2017 4:11	59	23/5/2017 5:16	61	24/5/2017 6:21	66	25/5/2017 23:26	61
22/5/2017 4:16	59	23/5/2017 5:21	61	24/5/2017 6:26	66	25/5/2017 23:31	61

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
Normal Day 07:00-19:00											
27/4/2017 7:01	60	4/5/2017 13:01	66	10/5/2017 7:31	62	15/5/2017 14:01	65	20/5/2017 8:31	63	25/5/2017 15:01	65
27/4/2017 7:31	60	4/5/2017 13:31	66	10/5/2017 8:01	63	15/5/2017 14:31	65	20/5/2017 9:01	67	25/5/2017 15:31	66
27/4/2017 8:01	60	4/5/2017 14:01	67	10/5/2017 8:31	64	15/5/2017 15:01	65	20/5/2017 9:31	66	25/5/2017 16:01	66
27/4/2017 8:31	61	4/5/2017 14:31	67	10/5/2017 9:01	65	15/5/2017 15:31	63	20/5/2017 10:01	66	25/5/2017 16:31	66
27/4/2017 9:01	64	4/5/2017 15:01	64	10/5/2017 9:31	65	15/5/2017 16:01	63	20/5/2017 10:31	66	25/5/2017 17:01	63
27/4/2017 9:31	67	4/5/2017 15:31	65	10/5/2017 10:01	68	15/5/2017 16:31	63	20/5/2017 11:01	65	25/5/2017 17:31	63
27/4/2017 10:01	67	4/5/2017 16:01	66	10/5/2017 10:31	52	15/5/2017 17:01	64	20/5/2017 11:31	63	25/5/2017 18:01	62
27/4/2017 10:31	65	4/5/2017 16:31	65	10/5/2017 11:01	67	15/5/2017 17:31	63	20/5/2017 12:01	62	25/5/2017 18:31	64
27/4/2017 11:01	64	4/5/2017 17:01	64	10/5/2017 11:31	65	15/5/2017 18:01	62	20/5/2017 12:31	62	26/5/2017 7:01	60
27/4/2017 11:31	63	4/5/2017 17:31	64	10/5/2017 12:01	63	15/5/2017 18:31	61	20/5/2017 13:01	64	26/5/2017 7:31	61
27/4/2017 12:01	61	4/5/2017 18:01	63	10/5/2017 12:31	64	16/5/2017 7:01	61	20/5/2017 13:31	65	26/5/2017 8:01	61
27/4/2017 12:31	61	4/5/2017 18:31	64	10/5/2017 13:01	66	16/5/2017 7:31	60	20/5/2017 14:01	67	26/5/2017 8:31	62
27/4/2017 13:01	63	5/5/2017 7:01	61	10/5/2017 13:31	66	16/5/2017 8:01	63	20/5/2017 14:31	67	26/5/2017 9:01	65
27/4/2017 13:31	66	5/5/2017 7:31	62	10/5/2017 14:01	64	16/5/2017 8:31	65	20/5/2017 15:01	66	26/5/2017 9:31	64
27/4/2017 14:01	64	5/5/2017 8:01	62	10/5/2017 14:31	65	16/5/2017 9:01	67	20/5/2017 15:31	66	26/5/2017 10:01	64
27/4/2017 14:31	66	5/5/2017 8:31	63	10/5/2017 15:01	66	16/5/2017 9:31	65	20/5/2017 16:01	66	26/5/2017 10:31	63
27/4/2017 15:01	65	5/5/2017 9:01	64	10/5/2017 15:31	64	16/5/2017 10:01	48	20/5/2017 16:31	66	26/5/2017 11:01	64
27/4/2017 15:31	65	5/5/2017 9:31	66	10/5/2017 16:01	64	16/5/2017 10:31	63	20/5/2017 17:01	64	26/5/2017 11:31	62
27/4/2017 16:01	65	5/5/2017 10:01	65	10/5/2017 16:31	65	16/5/2017 11:01	68	20/5/2017 17:31	63	26/5/2017 12:01	63
27/4/2017 16:31	63	5/5/2017 10:31	65	10/5/2017 17:01	64	16/5/2017 11:31	65	20/5/2017 18:01	64	26/5/2017 12:31	64
27/4/2017 17:01	62	5/5/2017 11:01	65	10/5/2017 17:31	62	16/5/2017 12:01	61	20/5/2017 18:31	62	26/5/2017 13:01	64
27/4/2017 17:31	61	5/5/2017 11:31	64	10/5/2017 18:01	64	16/5/2017 12:31	64	22/5/2017 7:01	64	26/5/2017 13:31	64
27/4/2017 18:01	61	5/5/2017 12:01	62	10/5/2017 18:31	62	16/5/2017 13:01	68	22/5/2017 7:31	65	26/5/2017 14:01	64
27/4/2017 18:31	61	5/5/2017 12:31	63	11/5/2017 7:01	61	16/5/2017 13:31	66	22/5/2017 8:01	62	26/5/2017 14:31	64
28/4/2017 7:01	61	5/5/2017 13:01	65	11/5/2017 7:31	62	16/5/2017 14:01	67	22/5/2017 8:31	63	26/5/2017 15:01	63
28/4/2017 7:31	61	5/5/2017 13:31	65	11/5/2017 8:01	62	16/5/2017 14:31	66	22/5/2017 9:01	64	26/5/2017 15:31	64
28/4/2017 8:01	62	5/5/2017 14:01	65	11/5/2017 8:31	66	16/5/2017 15:01	66	22/5/2017 9:31	65	26/5/2017 16:01	64
28/4/2017 8:31	62	5/5/2017 14:31	66	11/5/2017 9:01	68	16/5/2017 15:31	67	22/5/2017 10:01	65	26/5/2017 16:31	63
28/4/2017 9:01	65	5/5/2017 15:01	65	11/5/2017 9:31	68	16/5/2017 16:01	66	22/5/2017 10:31	65	26/5/2017 17:01	64
28/4/2017 9:31	65	5/5/2017 15:31	66	11/5/2017 10:01	67	16/5/2017 16:31	67	22/5/2017 11:01	65	26/5/2017 17:31	63
28/4/2017 10:01	65	5/5/2017 16:01	65	11/5/2017 10:31	67	16/5/2017 17:01	67	22/5/2017 11:31	63	26/5/2017 18:01	62
28/4/2017 10:31	64	5/5/2017 16:31	64	11/5/2017 11:01	66	16/5/2017 17:31	64	22/5/2017 12:01	63	26/5/2017 18:31	61
28/4/2017 11:01	64	5/5/2017 17:01	64	11/5/2017 11:31	63	16/5/2017 18:01	63	22/5/2017 12:31	63		
28/4/2017 11:31	62	5/5/2017 17:31	65	11/5/2017 12:01	61	16/5/2017 18:31	62	22/5/2017 13:01	66	Normal Day 19:00-23:00 Sunday & Holiday 07:00-23:00	
28/4/2017 12:01	62	5/5/2017 18:01	63	11/5/2017 12:31	61	17/5/2017 7:01	60	22/5/2017 13:31	66		
28/4/2017 12:31	62	5/5/2017 18:31	61	11/5/2017 13:01	65	17/5/2017 7:31	60	22/5/2017 14:01	65	27/4/2017 19:01	60
28/4/2017 13:01	65	6/5/2017 7:01	60	11/5/2017 13:31	67	17/5/2017 8:01	62	22/5/2017 14:31	66	27/4/2017 19:31	61
28/4/2017 13:31	66	6/5/2017 7:31	61	11/5/2017 14:01	67	17/5/2017 8:31	65	22/5/2017 15:01	66	27/4/2017 19:51	60
28/4/2017 14:01	67	6/5/2017 8:01	62	11/5/2017 14:31	67	17/5/2017 9:01	67	22/5/2017 15:31	66	27/4/2017 20:01	60
28/4/2017 14:31	67	6/5/2017 8:31	63	11/5/2017 15:01	66	17/5/2017 9:31	66	22/5/2017 16:01	66	27/4/2017 20:11	61
28/4/2017 15:01	66	6/5/2017 9:01	66	11/5/2017 15:31	67	17/5/2017 10:01	59	22/5/2017 16:31	65	27/4/2017 20:21	62
28/4/2017 15:31	65	6/5/2017 9:31	65	11/5/2017 16:01	66	17/5/2017 10:31	68	22/5/2017 17:01	65	27/4/2017 20:31	61
28/4/2017 16:01	65	6/5/2017 10:01	65	11/5/2017 16:31	65	17/5/2017 11:01	67	22/5/2017 17:31	64	27/4/2017 20:41	61
28/4/2017 16:31	66	6/5/2017 10:31	64	11/5/2017 17:01	65	17/5/2017 11:31	64	22/5/2017 18:01	64	27/4/2017 20:51	61
28/4/2017 17:01	64	6/5/2017 11:01	65	11/5/2017 17:31	61	17/5/2017 12:01	63	22/5/2017 18:31	62	27/4/2017 21:01	61
28/4/2017 17:31	62	6/5/2017 11:31	62	11/5/2017 18:01	62	17/5/2017 12:31	64	23/5/2017 7:01	55	27/4/2017 21:11	60
28/4/2017 18:01	61	6/5/2017 12:01	60	11/5/2017 18:31	62	17/5/2017 13:01	66	23/5/2017 7:31	58	27/4/2017 21:21	62
28/4/2017 18:31	62	6/5/2017 12:31	61	12/5/2017 7:01	60	17/5/2017 13:31	66	23/5/2017 8:01	51	27/4/2017 21:31	60
29/4/2017 7:01	61	6/5/2017 13:01	63	12/5/2017 7:31	60	17/5/2017 14:01	66	23/5/2017 8:31	67	27/4/2017 21:41	61
29/4/2017 7:31	62	6/5/2017 13:31	64	12/5/2017 8:01	63	17/5/2017 14:31	65	23/5/2017 9:01	65	27/4/2017 21:51	60
29/4/2017 8:01	62	6/5/2017 14:01	66	12/5/2017 8:31	66	17/5/2017 15:01	66	23/5/2017 9:31	68	27/4/2017 22:01	60
29/4/2017 8:31	66	6/5/2017 14:31	65	12/5/2017 9:01	65	17/5/2017 15:31	66	23/5/2017 10:01	66	27/4/2017 22:11	60
29/4/2017 9:01	65	6/5/2017 15:01	63	12/5/2017 9:31	66	17/5/2017 16:01	66	23/5/2017 10:31	67	27/4/2017 22:21	60
29/4/2017 9:31	66	6/5/2017 15:31	64	12/5/2017 10:01	66	17/5/2017 16:31	65	23/5/2017 11:01	66	27/4/2017 22:31	60
29/4/2017 10:01	67	6/5/2017 16:01	64	12/5/2017 10:31	66	17/5/2017 17:01	64	23/5/2017 11:31	64	27/4/2017 22:41	62
29/4/2017 10:31	68	6/5/2017 16:31	64	12/5/2017 11:01	66	17/5/2017 17:31	62	23/5/2017 12:01	62	27/4/2017 22:51	60
29/4/2017 11:01	67	6/5/2017 17:01	64	12/5/2017 11:31	62	17/5/2017 18:01	63	23/5/2017 12:31	62	27/4/2017 23:01	60
29/4/2017 11:31	63	6/5/2017 17:31	64	12/5/2017 12:01	62	17/5/2017 18:31	61	23/5/2017 13:01	64	27/4/2017 23:11	60
29/4/2017 12:01	61	6/5/2017 18:01	63	12/5/2017 12:31	62	18/5/2017 7:01	60	23/5/2017 13:31	65	27/4/2017 23:21	62
29/4/2017 12:31	61	6/5/2017 18:31	61	12/5/2017 13:01	64	18/5/2017 7:31	60	23/5/2017 14:01	64	27/4/2017 23:31	60
29/4/2017 13:01	64	8/5/2017 7:01	61	12/5/2017 13:31	65	18/5/2017 8:01	62	23/5/2017 14:31	65	27/4/2017 23:41	61
29/4/2017 13:31	65	8/5/2017 7:31	62	12/5/2017 14:01	66	18/5/2017 8:31	63	23/5/2017 15:01	66	27/4/2017 23:51	61
29/4/2017 14:01	68	8/5/2017 8:01	65	12/5/2017 14:31	66	18/5/2017 9:01	65	23/5/2017 15:31	65	27/4/2017 24:01	61
29/4/2017 14:31	67	8/5/2017 8:31	63	12/5/2017 15:01	64	18/5/2017 9:31	67	23/5/2017 16:01	65	27/4/2017 24:11	60
29/4/2017 15:01	65	8/5/2017 9:01	65	12/5/2017 15:31	65	18/5/2017 10:01	67	23/5/2017 16:31	65	27/4/2017 24:21	60
29/4/2017 15:31	64	8/5/2017 9:31	64	12/5/2017 16:01	66	18/5/2017 10:31	67	23/5/2017 17:01	64	27/4/2017 24:31	60
29/4/2017 16:01	64	8/5/2017 10:01	64	12/5/2017 16:31	64	18/5/2017 11:01	66	23/5/2017 17:31	62	27/4/2017 24:41	61
29/4/2017 16:31	66	8/5/2017 10:31	64	12/5/2017 17:01	64	18/5/2017 11:31	63	23/5/2017 18:01	62	27/4/2017 24:51	61
29/4/2017 17:01	65	8/5/2017 11:01	64	12/5/2017 17:31	62	18/5/2017 12:01	62	23/5/2017 18:31	62	27/4/2017 25:01	61
29/4/2017 17:31	63	8/5/2017 11:31	63	12/5/2017 18:01	61	18/5/2017 12:31	62	24/5/2017 7:01	69	27/4/2017 25:11	61
29/4/2017 18:01	61	8/5/2017 12:01	61	12/5/2017 18:31	62	18/5/2017 13:01	65	24/5/2017 7:31	63	27/4/2017 25:21	60
29/4/2017 18:31	61	8/5/2017 12:31	62	13/5/2017 7:01	61	18/5/2017 13:31	65	24/5/2017 8:01	65	27/4/2017 25:31	60
2/5/2017 7:01	61	8/5/2017 13:01	63	13/5/2017 7:31	61	18/5/2017 14:01	65	24/5/2017 8:31	66	27/4/2017 25:41	60
2/5/2017 7:31	62	8/5/2017 13:31	65	13/5/2017 8:01	64	18/5/2017 14:31	67	24/5/2017 9			

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
28/4/2017 21:01	61	30/4/2017 10:06	60	30/4/2017 19:11	60	1/5/2017 12:16	60	1/5/2017 21:21	60	3/5/2017 10:26	62
28/4/2017 21:06	62	30/4/2017 10:11	63	30/4/2017 19:16	61	1/5/2017 12:21	61	1/5/2017 21:26	59	3/5/2017 10:31	62
28/4/2017 21:11	61	30/4/2017 10:16	61	30/4/2017 19:21	60	1/5/2017 12:26	61	1/5/2017 21:31	59	3/5/2017 10:36	51
28/4/2017 21:16	62	30/4/2017 10:21	60	30/4/2017 19:26	60	1/5/2017 12:31	60	1/5/2017 21:36	60	3/5/2017 10:41	62
28/4/2017 21:21	62	30/4/2017 10:26	62	30/4/2017 19:31	59	1/5/2017 12:36	61	1/5/2017 21:41	59	3/5/2017 10:46	61
28/4/2017 21:26	61	30/4/2017 10:31	59	30/4/2017 19:36	60	1/5/2017 12:41	60	1/5/2017 21:46	59	3/5/2017 10:51	60
28/4/2017 21:31	61	30/4/2017 10:36	61	30/4/2017 19:41	61	1/5/2017 12:46	61	1/5/2017 21:51	59	3/5/2017 10:56	61
28/4/2017 21:36	61	30/4/2017 10:41	60	30/4/2017 19:46	60	1/5/2017 12:51	61	1/5/2017 21:56	59	3/5/2017 11:01	61
28/4/2017 21:41	61	30/4/2017 10:46	60	30/4/2017 19:51	60	1/5/2017 12:56	61	1/5/2017 22:01	61	3/5/2017 11:06	62
28/4/2017 21:46	61	30/4/2017 10:51	59	30/4/2017 19:56	60	1/5/2017 13:01	61	1/5/2017 22:06	59	3/5/2017 11:11	62
28/4/2017 21:51	53	30/4/2017 10:56	61	30/4/2017 20:01	59	1/5/2017 13:06	61	1/5/2017 22:11	59	3/5/2017 11:16	61
28/4/2017 21:56	61	30/4/2017 11:01	60	30/4/2017 20:06	60	1/5/2017 13:11	61	1/5/2017 22:16	60	3/5/2017 11:21	61
28/4/2017 22:01	60	30/4/2017 11:06	59	30/4/2017 20:11	60	1/5/2017 13:16	61	1/5/2017 22:21	59	3/5/2017 11:26	60
28/4/2017 22:06	61	30/4/2017 11:11	59	30/4/2017 20:16	60	1/5/2017 13:21	61	1/5/2017 22:26	59	3/5/2017 11:31	61
28/4/2017 22:11	61	30/4/2017 11:16	59	30/4/2017 20:21	60	1/5/2017 13:26	60	1/5/2017 22:31	59	3/5/2017 11:36	61
28/4/2017 22:16	61	30/4/2017 11:21	60	30/4/2017 20:26	60	1/5/2017 13:31	62	1/5/2017 22:36	59	3/5/2017 11:41	62
28/4/2017 22:21	60	30/4/2017 11:26	59	30/4/2017 20:31	59	1/5/2017 13:36	55	1/5/2017 22:41	59	3/5/2017 11:46	60
28/4/2017 22:26	60	30/4/2017 11:31	59	30/4/2017 20:36	61	1/5/2017 13:41	61	1/5/2017 22:46	59	3/5/2017 11:51	61
28/4/2017 22:31	62	30/4/2017 11:36	60	30/4/2017 20:41	60	1/5/2017 13:46	61	1/5/2017 22:51	58	3/5/2017 11:56	61
28/4/2017 22:36	63	30/4/2017 11:41	60	30/4/2017 20:46	59	1/5/2017 13:51	61	1/5/2017 22:56	60	3/5/2017 12:01	63
28/4/2017 22:41	62	30/4/2017 11:46	60	30/4/2017 20:51	59	1/5/2017 13:56	62	2/5/2017 19:01	56	3/5/2017 12:06	60
28/4/2017 22:46	60	30/4/2017 11:51	60	30/4/2017 20:56	60	1/5/2017 14:01	62	2/5/2017 19:06	62	3/5/2017 12:11	61
28/4/2017 22:51	61	30/4/2017 11:56	59	30/4/2017 21:01	43	1/5/2017 14:06	60	2/5/2017 19:11	62	3/5/2017 12:16	60
28/4/2017 22:56	60	30/4/2017 12:01	60	30/4/2017 21:06	60	1/5/2017 14:11	61	2/5/2017 19:16	62	3/5/2017 12:21	62
29/4/2017 19:01	62	30/4/2017 12:06	60	30/4/2017 21:11	60	1/5/2017 14:16	61	2/5/2017 19:21	61	3/5/2017 12:26	61
29/4/2017 19:06	62	30/4/2017 12:11	60	30/4/2017 21:16	59	1/5/2017 14:21	60	2/5/2017 19:26	62	3/5/2017 12:31	61
29/4/2017 19:11	61	30/4/2017 12:16	60	30/4/2017 21:21	60	1/5/2017 14:26	61	2/5/2017 19:31	62	3/5/2017 12:36	61
29/4/2017 19:16	61	30/4/2017 12:21	60	30/4/2017 21:26	58	1/5/2017 14:31	63	2/5/2017 19:36	64	3/5/2017 12:41	61
29/4/2017 19:21	62	30/4/2017 12:26	59	30/4/2017 21:31	59	1/5/2017 14:36	61	2/5/2017 19:41	61	3/5/2017 12:46	62
29/4/2017 19:26	62	30/4/2017 12:31	60	30/4/2017 21:36	59	1/5/2017 14:41	61	2/5/2017 19:46	61	3/5/2017 12:51	61
29/4/2017 19:31	63	30/4/2017 12:36	60	30/4/2017 21:41	60	1/5/2017 14:46	61	2/5/2017 19:51	62	3/5/2017 12:56	62
29/4/2017 19:36	62	30/4/2017 12:41	61	30/4/2017 21:46	59	1/5/2017 14:51	61	2/5/2017 19:56	62	3/5/2017 13:01	62
29/4/2017 19:41	61	30/4/2017 12:46	60	30/4/2017 21:51	61	1/5/2017 14:56	61	2/5/2017 20:01	63	3/5/2017 13:06	62
29/4/2017 19:46	61	30/4/2017 12:51	61	30/4/2017 21:56	59	1/5/2017 15:01	61	2/5/2017 20:06	61	3/5/2017 13:11	61
29/4/2017 19:51	60	30/4/2017 12:56	61	30/4/2017 22:01	60	1/5/2017 15:06	61	2/5/2017 20:11	61	3/5/2017 13:16	61
29/4/2017 19:56	56	30/4/2017 13:01	60	30/4/2017 22:06	59	1/5/2017 15:11	62	2/5/2017 20:16	62	3/5/2017 13:21	61
29/4/2017 20:01	60	30/4/2017 13:06	60	30/4/2017 22:11	60	1/5/2017 15:16	61	2/5/2017 20:21	61	3/5/2017 13:26	62
29/4/2017 20:06	60	30/4/2017 13:11	60	30/4/2017 22:16	61	1/5/2017 15:21	62	2/5/2017 20:26	61	3/5/2017 13:31	62
29/4/2017 20:11	63	30/4/2017 13:16	59	30/4/2017 22:21	62	1/5/2017 15:26	61	2/5/2017 20:31	61	3/5/2017 13:36	62
29/4/2017 20:16	61	30/4/2017 13:21	60	30/4/2017 22:26	60	1/5/2017 15:31	61	2/5/2017 20:36	61	3/5/2017 13:41	63
29/4/2017 20:21	61	30/4/2017 13:26	60	30/4/2017 22:31	59	1/5/2017 15:36	62	2/5/2017 20:41	62	3/5/2017 13:46	62
29/4/2017 20:26	60	30/4/2017 13:31	60	30/4/2017 22:36	59	1/5/2017 15:41	61	2/5/2017 20:46	61	3/5/2017 13:51	61
29/4/2017 20:31	62	30/4/2017 13:36	60	30/4/2017 22:41	61	1/5/2017 15:46	61	2/5/2017 20:51	61	3/5/2017 13:56	62
29/4/2017 20:36	63	30/4/2017 13:41	61	30/4/2017 22:46	58	1/5/2017 15:51	61	2/5/2017 20:56	61	3/5/2017 14:01	61
29/4/2017 20:41	61	30/4/2017 13:46	61	30/4/2017 22:51	59	1/5/2017 15:56	61	2/5/2017 21:01	61	3/5/2017 14:06	58
29/4/2017 20:46	60	30/4/2017 13:51	60	30/4/2017 22:56	61	1/5/2017 16:01	61	2/5/2017 21:06	61	3/5/2017 14:11	61
29/4/2017 20:51	60	30/4/2017 13:56	60	1/5/2017 7:01	58	1/5/2017 16:06	61	2/5/2017 21:11	62	3/5/2017 14:16	61
29/4/2017 20:56	61	30/4/2017 14:01	61	1/5/2017 7:06	58	1/5/2017 16:11	61	2/5/2017 21:16	60	3/5/2017 14:21	61
29/4/2017 21:01	61	30/4/2017 14:06	61	1/5/2017 7:11	58	1/5/2017 16:16	62	2/5/2017 21:21	60	3/5/2017 14:26	61
29/4/2017 21:06	61	30/4/2017 14:11	61	1/5/2017 7:16	61	1/5/2017 16:21	61	2/5/2017 21:26	61	3/5/2017 14:31	59
29/4/2017 21:11	61	30/4/2017 14:16	61	1/5/2017 7:21	59	1/5/2017 16:26	61	2/5/2017 21:31	61	3/5/2017 14:36	59
29/4/2017 21:16	62	30/4/2017 14:21	60	1/5/2017 7:26	58	1/5/2017 16:31	62	2/5/2017 21:36	61	3/5/2017 14:41	60
29/4/2017 21:21	61	30/4/2017 14:26	60	1/5/2017 7:31	59	1/5/2017 16:36	60	2/5/2017 21:41	60	3/5/2017 14:46	61
29/4/2017 21:26	60	30/4/2017 14:31	61	1/5/2017 7:36	59	1/5/2017 16:41	61	2/5/2017 21:46	61	3/5/2017 14:51	63
29/4/2017 21:31	62	30/4/2017 14:36	61	1/5/2017 7:41	59	1/5/2017 16:46	61	2/5/2017 21:51	62	3/5/2017 14:56	62
29/4/2017 21:36	61	30/4/2017 14:41	61	1/5/2017 7:46	60	1/5/2017 16:51	61	2/5/2017 21:56	60	3/5/2017 15:01	62
29/4/2017 21:41	60	30/4/2017 14:46	60	1/5/2017 7:51	60	1/5/2017 16:56	61	2/5/2017 22:01	60	3/5/2017 15:06	62
29/4/2017 21:46	60	30/4/2017 14:51	61	1/5/2017 7:56	58	1/5/2017 17:01	61	2/5/2017 22:06	60	3/5/2017 15:11	57
29/4/2017 21:51	61	30/4/2017 14:56	61	1/5/2017 8:01	61	1/5/2017 17:06	60	2/5/2017 22:11	63	3/5/2017 15:16	60
29/4/2017 21:56	61	30/4/2017 15:01	61	1/5/2017 8:06	58	1/5/2017 17:11	60	2/5/2017 22:16	59	3/5/2017 15:21	61
29/4/2017 22:01	60	30/4/2017 15:06	60	1/5/2017 8:11	59	1/5/2017 17:16	60	2/5/2017 22:21	60	3/5/2017 15:26	61
29/4/2017 22:06	60	30/4/2017 15:11	61	1/5/2017 8:16	60	1/5/2017 17:21	61	2/5/2017 22:26	61	3/5/2017 15:31	62
29/4/2017 22:11	60	30/4/2017 15:16	61	1/5/2017 8:21	60	1/5/2017 17:26	62	2/5/2017 22:31	64	3/5/2017 15:36	60
29/4/2017 22:16	60	30/4/2017 15:21	61	1/5/2017 8:26	60	1/5/2017 17:31	61	2/5/2017 22:36	60	3/5/2017 15:41	61
29/4/2017 22:21	60	30/4/2017 15:26	62	1/5/2017 8:31	59	1/5/2017 17:36	61	2/5/2017 22:41	60	3/5/2017 15:46	60
29/4/2017 22:26	60	30/4/2017 15:31	60	1/5/2017 8:36	60	1/5/2017 17:41	61	2/5/2017 22:46	60	3/5/2017 15:51	60
29/4/2017 22:31	60	30/4/2017 15:36	61	1/5/2017 8:41	62	1/5/2017 17:46	61	2/5/2017 22:51	61	3/5/2017 15:56	59
29/4/2017 22:36	61	30/4/2017 15:41	61	1/5/2017 8:46	59	1/5/2017 17:51	61	2/5/2017 22:56	60	3/5/2017 16:01	63
29/4/2017 22:41	61	30/4/2017 15:46	60	1/5/2017 8:51	60	1/5/2017 17:56	61	3/5/2017 7:01	59	3/5/2017 16:06	61
29/4/2017 22:46	59	30/4/2017 15:51	61	1/5/2017 8:56	61	1/5/2017 18:01	63	3/5/2017 7:06	62	3/5/2017 16:11	61
29/4/2017 22:51	60	30/4/2017 15:56	61	1/5/2017 9:01	54	1/5/2017 18:06	60	3/5/2017 7:11	60	3/5/2017 16:16	62
29/4/2017 22:56	59	30/4/2017 16:01	61	1/5/2017 9:06	60	1/5/2017 18:11	60	3/5/2017 7:16	60	3/5/2017 16:21	62
30/4/2017 7:01	59	30/4/2017 16:06	62	1/5/2017 9:11	63	1/5/2017 18:16	62	3/5/2017 7:21	60	3/5/2017 16:26	57
30/4/2017 7:06	59	30/4/2017 16:11	61	1/5/2017 9:16	61	1/5/2017 18:21	58	3/5/2017 7:26	59	3/5/2017 16:31	59
30/4/2017 7:11	61	30/4/2017 16:16	63	1/5/2017 9:21	61	1/5/2017 18:26	61	3/5/2017 7:31	59		

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
3/5/2017 19:31	60	5/5/2017 20:36	61	7/5/2017 9:41	62	7/5/2017 18:46	61	9/5/2017 19:51	61	11/5/2017 20:56	61
3/5/2017 19:36	60	5/5/2017 20:41	61	7/5/2017 9:46	61	7/5/2017 18:51	62	9/5/2017 19:56	62	11/5/2017 21:01	62
3/5/2017 19:41	60	5/5/2017 20:46	61	7/5/2017 9:51	61	7/5/2017 18:56	61	9/5/2017 20:01	61	11/5/2017 21:06	61
3/5/2017 19:46	51	5/5/2017 20:51	61	7/5/2017 9:56	61	7/5/2017 19:01	61	9/5/2017 20:06	61	11/5/2017 21:11	60
3/5/2017 19:51	60	5/5/2017 20:56	61	7/5/2017 10:01	62	7/5/2017 19:06	62	9/5/2017 20:11	61	11/5/2017 21:16	61
3/5/2017 19:56	60	5/5/2017 21:01	60	7/5/2017 10:06	63	7/5/2017 19:11	61	9/5/2017 20:16	62	11/5/2017 21:21	61
3/5/2017 20:01	60	5/5/2017 21:06	61	7/5/2017 10:11	62	7/5/2017 19:16	62	9/5/2017 20:21	61	11/5/2017 21:26	61
3/5/2017 20:06	59	5/5/2017 21:11	61	7/5/2017 10:16	63	7/5/2017 19:21	62	9/5/2017 20:26	61	11/5/2017 21:31	60
3/5/2017 20:11	59	5/5/2017 21:16	60	7/5/2017 10:21	62	7/5/2017 19:26	62	9/5/2017 20:31	61	11/5/2017 21:36	61
3/5/2017 20:16	59	5/5/2017 21:21	61	7/5/2017 10:26	62	7/5/2017 19:31	62	9/5/2017 20:36	61	11/5/2017 21:41	60
3/5/2017 20:21	60	5/5/2017 21:26	60	7/5/2017 10:31	62	7/5/2017 19:36	63	9/5/2017 20:41	60	11/5/2017 21:46	60
3/5/2017 20:26	60	5/5/2017 21:31	60	7/5/2017 10:36	62	7/5/2017 19:41	63	9/5/2017 20:46	61	11/5/2017 21:51	60
3/5/2017 20:31	60	5/5/2017 21:36	60	7/5/2017 10:41	63	7/5/2017 19:46	63	9/5/2017 20:51	61	11/5/2017 21:56	59
3/5/2017 20:36	59	5/5/2017 21:41	60	7/5/2017 10:46	62	7/5/2017 19:51	63	9/5/2017 20:56	61	11/5/2017 22:01	60
3/5/2017 20:41	59	5/5/2017 21:46	60	7/5/2017 10:51	62	7/5/2017 19:56	62	9/5/2017 21:01	61	11/5/2017 22:06	60
3/5/2017 20:46	60	5/5/2017 21:51	60	7/5/2017 10:56	62	7/5/2017 20:01	62	9/5/2017 21:06	61	11/5/2017 22:11	61
3/5/2017 20:51	59	5/5/2017 21:56	59	7/5/2017 11:01	62	7/5/2017 20:06	62	9/5/2017 21:11	61	11/5/2017 22:16	60
3/5/2017 20:56	59	5/5/2017 22:01	60	7/5/2017 11:06	61	7/5/2017 20:11	62	9/5/2017 21:16	61	11/5/2017 22:21	61
3/5/2017 21:01	60	5/5/2017 22:06	59	7/5/2017 11:11	62	7/5/2017 20:16	63	9/5/2017 21:21	61	11/5/2017 22:26	60
3/5/2017 21:06	59	5/5/2017 22:11	60	7/5/2017 11:16	62	7/5/2017 20:21	62	9/5/2017 21:26	61	11/5/2017 22:31	60
3/5/2017 21:11	59	5/5/2017 22:16	60	7/5/2017 11:21	62	7/5/2017 20:26	62	9/5/2017 21:31	61	11/5/2017 22:36	61
3/5/2017 21:16	59	5/5/2017 22:21	60	7/5/2017 11:26	62	7/5/2017 20:31	61	9/5/2017 21:36	61	11/5/2017 22:41	60
3/5/2017 21:21	59	5/5/2017 22:26	63	7/5/2017 11:31	62	7/5/2017 20:36	63	9/5/2017 21:41	63	11/5/2017 22:46	60
3/5/2017 21:26	59	5/5/2017 22:31	60	7/5/2017 11:36	62	7/5/2017 20:41	61	9/5/2017 21:46	61	11/5/2017 22:51	60
3/5/2017 21:31	59	5/5/2017 22:36	61	7/5/2017 11:41	63	7/5/2017 20:46	62	9/5/2017 21:51	61	11/5/2017 22:56	60
3/5/2017 21:36	60	5/5/2017 22:41	60	7/5/2017 11:46	61	7/5/2017 20:51	62	9/5/2017 21:56	60	12/5/2017 19:01	61
3/5/2017 21:41	60	5/5/2017 22:46	60	7/5/2017 11:51	61	7/5/2017 20:56	62	9/5/2017 22:01	60	12/5/2017 19:06	61
3/5/2017 21:46	60	5/5/2017 22:51	60	7/5/2017 11:56	62	7/5/2017 21:01	61	9/5/2017 22:06	60	12/5/2017 19:11	61
3/5/2017 21:51	60	5/5/2017 22:56	60	7/5/2017 12:01	62	7/5/2017 21:06	62	9/5/2017 22:11	60	12/5/2017 19:16	61
3/5/2017 21:56	60	6/5/2017 19:01	62	7/5/2017 12:06	61	7/5/2017 21:11	62	9/5/2017 22:16	60	12/5/2017 19:21	61
3/5/2017 22:01	59	6/5/2017 19:06	60	7/5/2017 12:11	64	7/5/2017 21:16	62	9/5/2017 22:21	60	12/5/2017 19:26	61
3/5/2017 22:06	60	6/5/2017 19:11	61	7/5/2017 12:16	62	7/5/2017 21:21	62	9/5/2017 22:26	60	12/5/2017 19:31	61
3/5/2017 22:11	60	6/5/2017 19:16	61	7/5/2017 12:21	61	7/5/2017 21:26	62	9/5/2017 22:31	60	12/5/2017 19:36	60
3/5/2017 22:16	63	6/5/2017 19:21	62	7/5/2017 12:26	61	7/5/2017 21:31	62	9/5/2017 22:36	60	12/5/2017 19:41	60
3/5/2017 22:21	60	6/5/2017 19:26	61	7/5/2017 12:31	62	7/5/2017 21:36	62	9/5/2017 22:41	60	12/5/2017 19:46	60
3/5/2017 22:26	61	6/5/2017 19:31	61	7/5/2017 12:36	62	7/5/2017 21:41	62	9/5/2017 22:46	55	12/5/2017 19:51	60
3/5/2017 22:31	58	6/5/2017 19:36	61	7/5/2017 12:41	63	7/5/2017 21:46	62	9/5/2017 22:51	60	12/5/2017 19:56	60
3/5/2017 22:36	59	6/5/2017 19:41	61	7/5/2017 12:46	51	7/5/2017 21:51	62	9/5/2017 22:56	59	12/5/2017 20:01	61
3/5/2017 22:41	59	6/5/2017 19:46	60	7/5/2017 12:51	62	7/5/2017 21:56	62	10/5/2017 19:01	63	12/5/2017 20:06	61
3/5/2017 22:46	58	6/5/2017 19:51	61	7/5/2017 12:56	62	7/5/2017 22:01	62	10/5/2017 19:06	63	12/5/2017 20:11	62
3/5/2017 22:51	63	6/5/2017 19:56	61	7/5/2017 13:01	62	7/5/2017 22:06	62	10/5/2017 19:11	37	12/5/2017 20:16	61
3/5/2017 22:56	58	6/5/2017 20:01	61	7/5/2017 13:06	62	7/5/2017 22:11	62	10/5/2017 19:16	62	12/5/2017 20:21	62
4/5/2017 19:01	63	6/5/2017 20:06	61	7/5/2017 13:11	62	7/5/2017 22:16	62	10/5/2017 19:21	62	12/5/2017 20:26	61
4/5/2017 19:06	63	6/5/2017 20:11	61	7/5/2017 13:16	62	7/5/2017 22:21	62	10/5/2017 19:26	62	12/5/2017 20:31	61
4/5/2017 19:11	63	6/5/2017 20:16	60	7/5/2017 13:21	62	7/5/2017 22:26	62	10/5/2017 19:31	64	12/5/2017 20:36	62
4/5/2017 19:16	62	6/5/2017 20:21	60	7/5/2017 13:26	62	7/5/2017 22:31	62	10/5/2017 19:36	62	12/5/2017 20:41	61
4/5/2017 19:21	63	6/5/2017 20:26	61	7/5/2017 13:31	61	7/5/2017 22:36	62	10/5/2017 19:41	62	12/5/2017 20:46	61
4/5/2017 19:26	63	6/5/2017 20:31	60	7/5/2017 13:36	61	7/5/2017 22:41	62	10/5/2017 19:46	62	12/5/2017 20:51	61
4/5/2017 19:31	63	6/5/2017 20:36	61	7/5/2017 13:41	55	7/5/2017 22:46	62	10/5/2017 19:51	63	12/5/2017 20:56	61
4/5/2017 19:36	63	6/5/2017 20:41	60	7/5/2017 13:46	61	7/5/2017 22:51	62	10/5/2017 19:56	63	12/5/2017 21:01	61
4/5/2017 19:41	63	6/5/2017 20:46	61	7/5/2017 13:51	47	7/5/2017 22:56	62	10/5/2017 20:01	62	12/5/2017 21:06	61
4/5/2017 19:46	62	6/5/2017 20:51	60	7/5/2017 13:56	61	8/5/2017 19:01	62	10/5/2017 20:06	63	12/5/2017 21:11	61
4/5/2017 19:51	62	6/5/2017 20:56	62	7/5/2017 14:01	61	8/5/2017 19:06	56	10/5/2017 20:11	62	12/5/2017 21:16	61
4/5/2017 19:56	62	6/5/2017 21:01	61	7/5/2017 14:06	62	8/5/2017 19:11	62	10/5/2017 20:16	54	12/5/2017 21:21	60
4/5/2017 20:01	62	6/5/2017 21:06	61	7/5/2017 14:11	62	8/5/2017 19:16	61	10/5/2017 20:21	62	12/5/2017 21:26	60
4/5/2017 20:06	62	6/5/2017 21:11	63	7/5/2017 14:16	55	8/5/2017 19:21	62	10/5/2017 20:26	63	12/5/2017 21:31	61
4/5/2017 20:11	62	6/5/2017 21:16	61	7/5/2017 14:21	61	8/5/2017 19:26	61	10/5/2017 20:31	62	12/5/2017 21:36	60
4/5/2017 20:16	63	6/5/2017 21:21	60	7/5/2017 14:26	58	8/5/2017 19:31	61	10/5/2017 20:36	63	12/5/2017 21:41	60
4/5/2017 20:21	62	6/5/2017 21:26	60	7/5/2017 14:31	53	8/5/2017 19:36	63	10/5/2017 20:41	62	12/5/2017 21:46	59
4/5/2017 20:26	62	6/5/2017 21:31	60	7/5/2017 14:36	62	8/5/2017 19:41	61	10/5/2017 20:46	62	12/5/2017 21:51	60
4/5/2017 20:31	62	6/5/2017 21:36	60	7/5/2017 14:41	63	8/5/2017 19:46	61	10/5/2017 20:51	62	12/5/2017 21:56	60
4/5/2017 20:36	62	6/5/2017 21:41	61	7/5/2017 14:46	63	8/5/2017 19:51	62	10/5/2017 20:56	62	12/5/2017 22:01	61
4/5/2017 20:41	62	6/5/2017 21:46	61	7/5/2017 14:51	57	8/5/2017 19:56	62	10/5/2017 21:01	62	12/5/2017 22:06	60
4/5/2017 20:46	61	6/5/2017 21:51	62	7/5/2017 14:56	57	8/5/2017 20:01	62	10/5/2017 21:06	62	12/5/2017 22:11	62
4/5/2017 20:51	62	6/5/2017 21:56	64	7/5/2017 15:01	59	8/5/2017 20:06	61	10/5/2017 21:11	62	12/5/2017 22:16	62
4/5/2017 20:56	62	6/5/2017 22:01	62	7/5/2017 15:06	58	8/5/2017 20:11	62	10/5/2017 21:16	62	12/5/2017 22:21	61
4/5/2017 21:01	62	6/5/2017 22:06	62	7/5/2017 15:11	55	8/5/2017 20:16	61	10/5/2017 21:21	62	12/5/2017 22:26	60
4/5/2017 21:06	61	6/5/2017 22:11	60	7/5/2017 15:16	61	8/5/2017 20:21	62	10/5/2017 21:26	61	12/5/2017 22:31	61
4/5/2017 21:11	62	6/5/2017 22:16	61	7/5/2017 15:21	61	8/5/2017 20:26	61	10/5/2017 21:31	61	12/5/2017 22:36	62
4/5/2017 21:16	61	6/5/2017 22:21	60	7/5/2017 15:26	61	8/5/2017 20:31	62	10/5/2017 21:36	61	12/5/2017 22:41	60
4/5/2017 21:21	62	6/5/2017 22:26	60	7/5/2017 15:31	64	8/5/2017 20:36	61	10/5/2017 21:41	62	12/5/2017 22:46	60
4/5/2017 21:26	62	6/5/2017 22:31	60	7/5/2017 15:36	57	8/5/2017 20:41	60	10/5/2017 21:46	62	12/5/2017 22:51	61
4/5/2017 21:31	62	6/5/2017 22:36	60	7/5/2017 15:41	60	8/5/2017 20:46	61	10/5/2017 21:51	62	12/5/2017 22:56	61
4/5/2017 21:36	61	6/5/2017 22:41	60	7/5/2017 15:46	58	8/5/2017 20:51	62	10/5/2017 21:56	62	13/5/2017 19:01	59
4/5/2017 21:41	62	6/5/2017 22:46	59	7/5/2017 15:51	59	8/5/2017 20:56	61	10/5/2017 22:01	62	13/5/2017 19:06	60
4/5/2017 21:46	62	6/5/2017 22:5									

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)							
13/5/2017 22:01	61	14/5/2017 15:06	62	15/5/2017 20:11	60	17/5/2017 21:16	60	19/5/2017 22:21	60
13/5/2017 22:06	61	14/5/2017 15:11	62	15/5/2017 20:16	61	17/5/2017 21:21	60	19/5/2017 22:26	60
13/5/2017 22:11	60	14/5/2017 15:16	61	15/5/2017 20:21	60	17/5/2017 21:26	59	19/5/2017 22:31	60
13/5/2017 22:16	62	14/5/2017 15:21	61	15/5/2017 20:26	61	17/5/2017 21:31	60	19/5/2017 22:36	60
13/5/2017 22:21	61	14/5/2017 15:26	61	15/5/2017 20:31	61	17/5/2017 21:36	60	19/5/2017 22:41	60
13/5/2017 22:26	62	14/5/2017 15:31	61	15/5/2017 20:36	60	17/5/2017 21:41	60	19/5/2017 22:46	60
13/5/2017 22:31	61	14/5/2017 15:36	61	15/5/2017 20:41	61	17/5/2017 21:46	60	19/5/2017 22:51	60
13/5/2017 22:36	61	14/5/2017 15:41	61	15/5/2017 20:46	60	17/5/2017 21:51	61	19/5/2017 22:56	60
13/5/2017 22:41	62	14/5/2017 15:46	62	15/5/2017 20:51	60	17/5/2017 21:56	61	20/5/2017 19:01	62
13/5/2017 22:46	61	14/5/2017 15:51	62	15/5/2017 20:56	61	17/5/2017 22:01	61	20/5/2017 19:06	63
13/5/2017 22:51	61	14/5/2017 15:56	63	15/5/2017 21:01	60	17/5/2017 22:06	61	20/5/2017 19:11	62
13/5/2017 22:56	59	14/5/2017 16:01	61	15/5/2017 21:06	61	17/5/2017 22:11	60	20/5/2017 19:16	62
14/5/2017 7:01	58	14/5/2017 16:06	61	15/5/2017 21:11	60	17/5/2017 22:16	62	20/5/2017 19:21	63
14/5/2017 7:06	60	14/5/2017 16:11	62	15/5/2017 21:16	60	17/5/2017 22:21	60	20/5/2017 19:26	63
14/5/2017 7:11	60	14/5/2017 16:16	62	15/5/2017 21:21	60	17/5/2017 22:26	60	20/5/2017 19:31	63
14/5/2017 7:16	60	14/5/2017 16:21	61	15/5/2017 21:26	60	17/5/2017 22:31	61	20/5/2017 19:36	63
14/5/2017 7:21	59	14/5/2017 16:26	62	15/5/2017 21:31	60	17/5/2017 22:36	62	20/5/2017 19:41	63
14/5/2017 7:26	59	14/5/2017 16:31	63	15/5/2017 21:36	60	17/5/2017 22:41	61	20/5/2017 19:46	63
14/5/2017 7:31	60	14/5/2017 16:36	62	15/5/2017 21:41	61	17/5/2017 22:46	60	20/5/2017 19:51	63
14/5/2017 7:36	62	14/5/2017 16:41	63	15/5/2017 21:46	61	17/5/2017 22:51	60	20/5/2017 19:56	63
14/5/2017 7:41	59	14/5/2017 16:46	62	15/5/2017 21:51	60	17/5/2017 22:56	60	20/5/2017 20:01	57
14/5/2017 7:46	64	14/5/2017 16:51	63	15/5/2017 21:56	60	18/5/2017 19:01	54	20/5/2017 20:06	49
14/5/2017 7:51	61	14/5/2017 16:56	63	15/5/2017 22:01	61	18/5/2017 19:06	62	20/5/2017 20:11	63
14/5/2017 7:56	60	14/5/2017 17:01	63	15/5/2017 22:06	63	18/5/2017 19:11	59	20/5/2017 20:16	63
14/5/2017 8:01	60	14/5/2017 17:06	62	15/5/2017 22:11	60	18/5/2017 19:16	59	20/5/2017 20:21	63
14/5/2017 8:06	60	14/5/2017 17:11	62	15/5/2017 22:16	61	18/5/2017 19:21	59	20/5/2017 20:26	63
14/5/2017 8:11	62	14/5/2017 17:16	61	15/5/2017 22:21	59	18/5/2017 19:26	53	20/5/2017 20:31	62
14/5/2017 8:16	61	14/5/2017 17:21	61	15/5/2017 22:26	60	18/5/2017 19:31	62	20/5/2017 20:36	62
14/5/2017 8:21	60	14/5/2017 17:26	63	15/5/2017 22:31	60	18/5/2017 19:36	59	20/5/2017 20:41	62
14/5/2017 8:26	61	14/5/2017 17:31	62	15/5/2017 22:36	60	18/5/2017 19:41	58	20/5/2017 20:46	63
14/5/2017 8:31	61	14/5/2017 17:36	62	15/5/2017 22:41	60	18/5/2017 19:46	63	20/5/2017 20:51	63
14/5/2017 8:36	60	14/5/2017 17:41	62	15/5/2017 22:46	60	18/5/2017 19:51	61	20/5/2017 20:56	62
14/5/2017 8:41	61	14/5/2017 17:46	61	15/5/2017 22:51	60	18/5/2017 19:56	62	20/5/2017 21:01	63
14/5/2017 8:46	61	14/5/2017 17:51	60	15/5/2017 22:56	60	18/5/2017 20:01	63	20/5/2017 21:06	62
14/5/2017 8:51	60	14/5/2017 17:56	61	16/5/2017 19:01	62	18/5/2017 20:06	59	20/5/2017 21:11	63
14/5/2017 8:56	60	14/5/2017 18:01	62	16/5/2017 19:06	60	18/5/2017 20:11	64	20/5/2017 21:16	62
14/5/2017 9:01	60	14/5/2017 18:06	60	16/5/2017 19:11	63	18/5/2017 20:16	62	20/5/2017 21:21	62
14/5/2017 9:06	62	14/5/2017 18:11	61	16/5/2017 19:16	64	18/5/2017 20:21	61	20/5/2017 21:26	63
14/5/2017 9:11	63	14/5/2017 18:16	60	16/5/2017 19:21	63	18/5/2017 20:26	61	20/5/2017 21:31	62
14/5/2017 9:16	60	14/5/2017 18:21	61	16/5/2017 19:26	62	18/5/2017 20:31	61	20/5/2017 21:36	56
14/5/2017 9:21	61	14/5/2017 18:26	60	16/5/2017 19:31	63	18/5/2017 20:36	61	20/5/2017 21:41	63
14/5/2017 9:26	61	14/5/2017 18:31	61	16/5/2017 19:36	63	18/5/2017 20:41	61	20/5/2017 21:46	62
14/5/2017 9:31	61	14/5/2017 18:36	61	16/5/2017 19:41	63	18/5/2017 20:46	62	20/5/2017 21:51	47
14/5/2017 9:36	61	14/5/2017 18:41	61	16/5/2017 19:46	63	18/5/2017 20:51	61	20/5/2017 21:56	62
14/5/2017 9:41	62	14/5/2017 18:46	62	16/5/2017 19:51	63	18/5/2017 20:56	61	20/5/2017 22:01	63
14/5/2017 9:46	60	14/5/2017 18:51	61	16/5/2017 19:56	63	18/5/2017 21:01	61	20/5/2017 22:06	62
14/5/2017 9:51	60	14/5/2017 18:56	63	16/5/2017 20:01	57	18/5/2017 21:06	61	20/5/2017 22:11	62
14/5/2017 9:56	61	14/5/2017 19:01	54	16/5/2017 20:06	62	18/5/2017 21:11	62	20/5/2017 22:16	62
14/5/2017 10:01	61	14/5/2017 19:06	57	16/5/2017 20:11	63	18/5/2017 21:16	62	20/5/2017 22:21	62
14/5/2017 10:06	61	14/5/2017 19:11	63	16/5/2017 20:16	63	18/5/2017 21:21	61	20/5/2017 22:26	62
14/5/2017 10:11	61	14/5/2017 19:16	63	16/5/2017 20:21	51	18/5/2017 21:26	60	20/5/2017 22:31	62
14/5/2017 10:16	61	14/5/2017 19:21	45	16/5/2017 20:26	63	18/5/2017 21:31	60	20/5/2017 22:36	62
14/5/2017 10:21	63	14/5/2017 19:26	62	16/5/2017 20:31	63	18/5/2017 21:36	61	20/5/2017 22:41	62
14/5/2017 10:26	62	14/5/2017 19:31	61	16/5/2017 20:36	63	18/5/2017 21:41	61	20/5/2017 22:46	62
14/5/2017 10:31	62	14/5/2017 19:36	62	16/5/2017 20:41	63	18/5/2017 21:46	61	20/5/2017 22:51	62
14/5/2017 10:36	61	14/5/2017 19:41	62	16/5/2017 20:46	63	18/5/2017 21:51	61	20/5/2017 22:56	62
14/5/2017 10:41	61	14/5/2017 19:46	61	16/5/2017 20:51	63	18/5/2017 21:56	61	21/5/2017 7:01	57
14/5/2017 10:46	61	14/5/2017 19:51	61	16/5/2017 20:56	62	18/5/2017 22:01	60	21/5/2017 7:06	59
14/5/2017 10:51	60	14/5/2017 19:56	61	16/5/2017 21:01	62	18/5/2017 22:06	60	21/5/2017 7:11	61
14/5/2017 10:56	61	14/5/2017 20:01	61	16/5/2017 21:06	61	18/5/2017 22:11	59	21/5/2017 7:16	58
14/5/2017 11:01	60	14/5/2017 20:06	61	16/5/2017 21:11	63	18/5/2017 22:16	61	21/5/2017 7:21	60
14/5/2017 11:06	60	14/5/2017 20:11	61	16/5/2017 21:16	62	18/5/2017 22:21	59	21/5/2017 7:26	58
14/5/2017 11:11	61	14/5/2017 20:16	61	16/5/2017 21:21	61	18/5/2017 22:26	60	21/5/2017 7:31	56
14/5/2017 11:16	61	14/5/2017 20:21	60	16/5/2017 21:26	61	18/5/2017 22:31	60	21/5/2017 7:36	57
14/5/2017 11:21	61	14/5/2017 20:26	61	16/5/2017 21:31	61	18/5/2017 22:36	60	21/5/2017 7:41	58
14/5/2017 11:26	60	14/5/2017 20:31	61	16/5/2017 21:36	61	18/5/2017 22:41	60	21/5/2017 7:46	57
14/5/2017 11:31	60	14/5/2017 20:36	63	16/5/2017 21:41	61	18/5/2017 22:46	60	21/5/2017 7:51	58
14/5/2017 11:36	61	14/5/2017 20:41	62	16/5/2017 21:46	61	18/5/2017 22:51	60	21/5/2017 7:56	58
14/5/2017 11:41	60	14/5/2017 20:46	63	16/5/2017 21:51	61	18/5/2017 22:56	59	21/5/2017 8:01	57
14/5/2017 11:46	60	14/5/2017 20:51	62	16/5/2017 21:56	61	19/5/2017 19:01	61	21/5/2017 8:06	57
14/5/2017 11:51	60	14/5/2017 20:56	60	16/5/2017 22:01	61	19/5/2017 19:06	61	21/5/2017 8:11	58
14/5/2017 11:56	60	14/5/2017 21:01	60	16/5/2017 22:06	60	19/5/2017 19:11	56	21/5/2017 8:16	58
14/5/2017 12:01	60	14/5/2017 21:06	61	16/5/2017 22:11	61	19/5/2017 19:16	62	21/5/2017 8:21	59
14/5/2017 12:06	60	14/5/2017 21:11	61	16/5/2017 22:16	61	19/5/2017 19:21	61	21/5/2017 8:26	58
14/5/2017 12:11	60	14/5/2017 21:16	61	16/5/2017 22:21	60	19/5/2017 19:26	62	21/5/2017 8:31	59
14/5/2017 12:16	52	14/5/2017 21:21	61	16/5/2017 22:26	60	19/5/2017 19:31	62	21/5/2017 8:36	60
14/5/2017 12:21	60	14/5/2017 21:26	61	16/5/2017 22:31	60	19/5/2017 19:36	62	21/5/2017 8:41	62
14/5/2017 12:26	59	14/5/2017 21:31	62	16/5/2017 22:36	61	19/5/2017 19:41	61	21/5/2017 8:46	63
14/5/2017 12:31	61	14/5/2017 21:36	61	16/5/2017 22:41	60	19/5/2017 19:46	62	21/5/2017 8:51	63
14/5/2017 12:36	60	14/5/2017 21:41	61	16/5/2017 22:46	60	19/5/2017 19:51	62	21/5/2017 8:56	63
14/5/2017 12:41	61	14/5/2017 21:46	61	16/5/2017 22:51	60	19/5/2017 19:56	61	21/5/2017 9:01	65
14/5/2017 12:46	60	14/5/2017 21:51	61	16/5/2017 22:56	62	19/5/2017 20:01	62	21/5/2017 9:06	66
14/5/2017 12:51	61	14/5/2017 21:56	61	17/5/2017 19:01	62	19/5/2017 20:06	61	21/5/2017 9:11	65
14/5/2017 12:56	60	14/5/2017 22:01	62	17/5/2017 19:06	62	19/5/2017 20:11	62	21/5/2017 9:16	65
14/5/2017 13:01	60	14/5/2017 22:06	61	17/5/2017 19:11	61	19/5/2017 20:16	62	21/5/2017 9:21	65
14/5/2017 13:06	60	14/5/2017 22:11	62	17/5/2017 19:16	61	19/5/2017 20:21	61	21/5/2017 9:26	65
14/5/2017 13:11	60	14/5/2017 22:16	61	17/5/2017 19:21	62	19/5/2017 20:26	63	21/5/2017 9:31	65
14/5/2017 13:16	60	14/5/2017 22:21	61	17/5/2017 19:26	61	19/5/2017 20:31	61		

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)	
21/5/2017 20:31	64	23/5/2017 21:36	61
21/5/2017 20:36	61	23/5/2017 21:41	62
21/5/2017 20:41	60	23/5/2017 21:46	62
21/5/2017 20:46	61	23/5/2017 21:51	60
21/5/2017 20:51	61	23/5/2017 21:56	61
21/5/2017 20:56	60	23/5/2017 22:01	60
21/5/2017 21:01	60	23/5/2017 22:06	60
21/5/2017 21:06	59	23/5/2017 22:11	61
21/5/2017 21:11	59	23/5/2017 22:16	60
21/5/2017 21:16	58	23/5/2017 22:21	60
21/5/2017 21:21	58	23/5/2017 22:26	60
21/5/2017 21:26	58	23/5/2017 22:31	61
21/5/2017 21:31	58	23/5/2017 22:36	60
21/5/2017 21:36	57	23/5/2017 22:41	60
21/5/2017 21:41	60	23/5/2017 22:46	60
21/5/2017 21:46	58	23/5/2017 22:51	61
21/5/2017 21:51	63	23/5/2017 22:56	59
21/5/2017 21:56	64	24/5/2017 19:01	63
21/5/2017 22:01	64	24/5/2017 19:06	62
21/5/2017 22:06	64	24/5/2017 19:11	62
21/5/2017 22:11	64	24/5/2017 19:16	62
21/5/2017 22:16	58	24/5/2017 19:21	62
21/5/2017 22:21	56	24/5/2017 19:26	61
21/5/2017 22:26	57	24/5/2017 19:31	63
21/5/2017 22:31	55	24/5/2017 19:36	62
21/5/2017 22:36	54	24/5/2017 19:41	62
21/5/2017 22:41	54	24/5/2017 19:46	56
21/5/2017 22:46	56	24/5/2017 19:51	63
21/5/2017 22:51	47	24/5/2017 19:56	62
21/5/2017 22:56	64	24/5/2017 20:01	56
22/5/2017 19:01	63	24/5/2017 20:06	61
22/5/2017 19:06	43	24/5/2017 20:11	62
22/5/2017 19:11	63	24/5/2017 20:16	62
22/5/2017 19:16	63	24/5/2017 20:21	61
22/5/2017 19:21	63	24/5/2017 20:26	61
22/5/2017 19:26	63	24/5/2017 20:31	61
22/5/2017 19:31	63	24/5/2017 20:36	61
22/5/2017 19:36	63	24/5/2017 20:41	63
22/5/2017 19:41	63	24/5/2017 20:46	61
22/5/2017 19:46	63	24/5/2017 20:51	62
22/5/2017 19:51	63	24/5/2017 20:56	63
22/5/2017 19:56	63	24/5/2017 21:01	61
22/5/2017 20:01	63	24/5/2017 21:06	60
22/5/2017 20:06	63	24/5/2017 21:11	61
22/5/2017 20:11	63	24/5/2017 21:16	61
22/5/2017 20:16	63	24/5/2017 21:21	61
22/5/2017 20:21	63	24/5/2017 21:26	62
22/5/2017 20:26	63	24/5/2017 21:31	60
22/5/2017 20:31	63	24/5/2017 21:36	61
22/5/2017 20:36	63	24/5/2017 21:41	60
22/5/2017 20:41	63	24/5/2017 21:46	60
22/5/2017 20:46	63	24/5/2017 21:51	61
22/5/2017 20:51	63	24/5/2017 21:56	60
22/5/2017 20:56	63	24/5/2017 22:01	60
22/5/2017 21:01	63	24/5/2017 22:06	60
22/5/2017 21:06	63	24/5/2017 22:11	60
22/5/2017 21:11	63	24/5/2017 22:16	60
22/5/2017 21:16	63	24/5/2017 22:21	60
22/5/2017 21:21	63	24/5/2017 22:26	60
22/5/2017 21:26	63	24/5/2017 22:31	60
22/5/2017 21:31	63	24/5/2017 22:36	60
22/5/2017 21:36	63	24/5/2017 22:41	60
22/5/2017 21:41	62	24/5/2017 22:46	59
22/5/2017 21:46	63	24/5/2017 22:51	59
22/5/2017 21:51	63	24/5/2017 22:56	59
22/5/2017 21:56	63	25/5/2017 19:01	62
22/5/2017 22:01	63	25/5/2017 19:06	61
22/5/2017 22:06	62	25/5/2017 19:11	52
22/5/2017 22:11	63	25/5/2017 19:16	62
22/5/2017 22:16	58	25/5/2017 19:21	63
22/5/2017 22:21	57	25/5/2017 19:26	61
22/5/2017 22:26	57	25/5/2017 19:31	63
22/5/2017 22:31	54	25/5/2017 19:36	63
22/5/2017 22:36	64	25/5/2017 19:41	63
22/5/2017 22:41	63	25/5/2017 19:46	62
22/5/2017 22:46	62	25/5/2017 19:51	62
22/5/2017 22:51	62	25/5/2017 19:56	61
22/5/2017 22:56	62	25/5/2017 20:01	62
23/5/2017 19:01	62	25/5/2017 20:06	60
23/5/2017 19:06	62	25/5/2017 20:11	63
23/5/2017 19:11	62	25/5/2017 20:16	61
23/5/2017 19:16	62	25/5/2017 20:21	62
23/5/2017 19:21	62	25/5/2017 20:26	61
23/5/2017 19:26	63	25/5/2017 20:31	61
23/5/2017 19:31	62	25/5/2017 20:36	63
23/5/2017 19:36	61	25/5/2017 20:41	61
23/5/2017 19:41	63	25/5/2017 20:46	61
23/5/2017 19:46	61	25/5/2017 20:51	61
23/5/2017 19:51	61	25/5/2017 20:56	62
23/5/2017 19:56	61	25/5/2017 21:01	52
23/5/2017 20:01	61	25/5/2017 21:06	62
23/5/2017 20:06	61	25/5/2017 21:11	60
23/5/2017 20:11	61	25/5/2017 21:16	61
23/5/2017 20:16	61	25/5/2017 21:21	60
23/5/2017 20:21	61	25/5/2017 21:26	62
23/5/2017 20:26	61	25/5/2017 21:31	61
23/5/2017 20:31	61	25/5/2017 21:36	61
23/5/2017 20:36	61	25/5/2017 21:41	63
23/5/2017 20:41	61	25/5/2017 21:46	62
23/5/2017 20:46	61	25/5/2017 21:51	61
23/5/2017 20:51	61	25/5/2017 21:56	61
23/5/2017 20:56	61	25/5/2017 22:01	60
23/5/2017 21:01	61	25/5/2017 22:06	61
23/5/2017 21:06	60	25/5/2017 22:11	61
23/5/2017 21:11	61	25/5/2017 22:16	62
23/5/2017 21:16	61	25/5/2017 22:21	61
23/5/2017 21:21	62	25/5/2017 22:26	61
23/5/2017 21:26	61	25/5/2017 22:31	60
23/5/2017 21:31	61	25/5/2017 22:36	60
23/5/2017 21:36	57	25/5/2017 22:41	60
23/5/2017 21:41	60	25/5/2017 22:46	59
23/5/2017 21:46	58	25/5/2017 22:51	59
23/5/2017 21:51	60	25/5/2017 22:56	59
23/5/2017 21:56	60	26/5/2017 19:01	61
23/5/2017 22:01	60	26/5/2017 19:06	61
23/5/2017 22:06	60	26/5/2017 19:11	62
23/5/2017 22:11	61	26/5/2017 19:16	60
23/5/2017 22:16	60	26/5/2017 19:21	54
23/5/2017 22:21	60	26/5/2017 19:26	61
23/5/2017 22:26	60	26/5/2017 19:31	61
23/5/2017 22:31	61	26/5/2017 19:36	62
23/5/2017 22:36	60	26/5/2017 19:41	60
23/5/2017 22:41	60	26/5/2017 19:46	60
23/5/2017 22:46	60	26/5/2017 19:51	59
23/5/2017 22:51	61	26/5/2017 19:56	61
23/5/2017 22:56	59	26/5/2017 20:01	59
24/5/2017 19:01	63	26/5/2017 20:06	61
24/5/2017 19:06	62	26/5/2017 20:11	60
24/5/2017 19:11	62	26/5/2017 20:16	60
24/5/2017 19:16	62	26/5/2017 20:21	62
24/5/2017 19:21	62	26/5/2017 20:26	60
24/5/2017 19:26	61	26/5/2017 20:31	61
24/5/2017 19:31	63	26/5/2017 20:36	60
24/5/2017 19:36	62	26/5/2017 20:41	59
24/5/2017 19:41	62	26/5/2017 20:46	60
24/5/2017 19:46	56	26/5/2017 20:51	61
24/5/2017 19:51	63	26/5/2017 20:56	61
24/5/2017 19:56	62	26/5/2017 21:01	60
24/5/2017 20:01	56	26/5/2017 21:06	60
24/5/2017 20:06	61	26/5/2017 21:11	60
24/5/2017 20:11	62	26/5/2017 21:16	60
24/5/2017 20:16	62	26/5/2017 21:21	60
24/5/2017 20:21	61	26/5/2017 21:26	60
24/5/2017 20:26	61	26/5/2017 21:31	60
24/5/2017 20:31	61	26/5/2017 21:36	59
24/5/2017 20:36	61	26/5/2017 21:41	59
24/5/2017 20:41	63	26/5/2017 21:46	59
24/5/2017 20:46	61	26/5/2017 21:51	62
24/5/2017 20:51	62	26/5/2017 21:56	62
24/5/2017 20:56	63	26/5/2017 22:01	61
24/5/2017 21:01	61	26/5/2017 22:06	64
24/5/2017 21:06	60	26/5/2017 22:11	61
24/5/2017 21:11	61	26/5/2017 22:16	60
24/5/2017 21:16	61	26/5/2017 22:21	60
24/5/2017 21:21	61	26/5/2017 22:26	61
24/5/2017 21:26	62	26/5/2017 22:31	60
24/5/2017 21:31	60	26/5/2017 22:36	60
24/5/2017 21:36	61	26/5/2017 22:41	61
24/5/2017 21:41	60	26/5/2017 22:46	61
24/5/2017 21:46	60	26/5/2017 22:51	61
24/5/2017 21:51	61	26/5/2017 22:56	60
24/5/2017 21:56	60		
24/5/2017 22:01	60	Night time: 23:00-07:00	
24/5/2017 22:06	60	27/4/2017 0:01	58
24/5/2017 22:11	60	27/4/2017 0:06	58
24/5/2017 22:16	60	27/4/2017 0:11	58
24/5/2017 22:21	60	27/4/2017 0:16	58
24/5/2017 22:26	60	27/4/2017 0:21	58
24/5/2017 22:31	60	27/4/2017 0:26	58
24/5/2017 22:36	60	27/4/2017 0:31	58
24/5/2017 22:41	60	27/4/2017 0:36	57
24/5/2017 22:46	59	27/4/2017 0:41	57
24/5/2017 22:51	59	27/4/2017 0:46	58
24/5/2017 22:56	59	27/4/2017 0:51	56
25/5/2017 19:01	62	27/4/2017 0:56	57
25/5/2017 19:06	61	27/4/2017 1:01	57
25/5/2017 19:11	52	27/4/2017 1:06	57
25/5/2017 19:16	62	27/4/2017 1:11	57
25/5/2017 19:21	63	27/4/2017 1:16	55
25/5/2017 19:26	61	27/4/2017 1:21	58
25/5/2017 19:31	63	27/4/2017 1:26	56
25/5/2017 19:36	63	27/4/2017 1:31	56
25/5/2017 19:41	63	27/4/2017 1:36	57
25/5/2017 19:46	62	27/4/2017 1:41	57
25/5/2017 19:51	62	27/4/2017 1:46	57
25/5/2017 19:56	61	27/4/2017 1:51	56
25/5/2017 20:01	62	27/4/2017 1:56	56
25/5/2017 20:06	60	27/4/2017 2:01	56
25/5/2017 20:11	63	27/4/2017 2:06	56
25/5/2017 20:16	61	27/4/2017 2:11	56
25/5/2017 20:21	62	27/4/2017 2:16	55
25/5/2017 20:26	61	27/4/2017 2:21	55
25/5/2017 20:31	61	27/4/2017 2:26	56
25/5/2017 20:36	63	27/4/2017 2:31	55
25/5/2017 20:41	61	27/4/2017 2:36	55
25/5/2017 20:46	61	27/4/2017 2:41	55
25/5/2017 20:51	61	27/4/2017 2:46	55
25/5/2017 20:56	62	27/4/2017 2:51	56
25/5/2017 21:01	52	27/4/2017 2:56	54
25/5/2017 21:06	62	27/4/2017 3:01	55
25/5/2017 21:11	60	27/4/2017 3:06	55
25/5/2017 21:16	61	27/4/2017 3:11	56
25/5/2017 21:21	60	27/4/2017 3:16	55
25/5/2017 21:26	62	27/4/2017 3:21	55
25/5/2017 21:31	61	27/4/2017 3:26	54
25/5/2017 21:36	61	27/4/2017 3:31	55
25/5/2017 21:41	63	27/4/2017 3:36	55
25/5/2017 21:46	62	27/4/2017 3:41	56
25/5/2017 21:51	61	27/4/2017 3:46	55
25/5/2017			

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
30/4/2017 23:46	57	2/5/2017 0:51	57	3/5/2017 1:56	57	4/5/2017 3:01	55	5/5/2017 4:06	58	6/5/2017 5:11	56
30/4/2017 23:51	58	2/5/2017 0:56	57	3/5/2017 2:01	58	4/5/2017 3:06	54	5/5/2017 4:11	58	6/5/2017 5:16	56
30/4/2017 23:56	58	2/5/2017 1:01	56	3/5/2017 2:06	57	4/5/2017 3:11	55	5/5/2017 4:16	58	6/5/2017 5:21	57
1/5/2017 0:01	57	2/5/2017 1:06	55	3/5/2017 2:11	56	4/5/2017 3:16	55	5/5/2017 4:21	58	6/5/2017 5:26	56
1/5/2017 0:06	57	2/5/2017 1:11	56	3/5/2017 2:16	56	4/5/2017 3:21	55	5/5/2017 4:26	59	6/5/2017 5:31	56
1/5/2017 0:11	58	2/5/2017 1:16	57	3/5/2017 2:21	56	4/5/2017 3:26	55	5/5/2017 4:31	59	6/5/2017 5:36	57
1/5/2017 0:16	57	2/5/2017 1:21	56	3/5/2017 2:26	56	4/5/2017 3:31	55	5/5/2017 4:36	58	6/5/2017 5:41	57
1/5/2017 0:21	57	2/5/2017 1:26	55	3/5/2017 2:31	56	4/5/2017 3:36	55	5/5/2017 4:41	58	6/5/2017 5:46	58
1/5/2017 0:26	57	2/5/2017 1:31	56	3/5/2017 2:36	57	4/5/2017 3:41	55	5/5/2017 4:46	58	6/5/2017 5:51	58
1/5/2017 0:31	58	2/5/2017 1:36	58	3/5/2017 2:41	56	4/5/2017 3:46	54	5/5/2017 4:51	59	6/5/2017 5:56	58
1/5/2017 0:36	57	2/5/2017 1:41	55	3/5/2017 2:46	58	4/5/2017 3:51	53	5/5/2017 4:56	59	6/5/2017 6:01	58
1/5/2017 0:41	57	2/5/2017 1:46	55	3/5/2017 2:51	56	4/5/2017 3:56	54	5/5/2017 5:01	58	6/5/2017 6:06	59
1/5/2017 0:46	57	2/5/2017 1:51	54	3/5/2017 2:56	57	4/5/2017 4:01	55	5/5/2017 5:06	58	6/5/2017 6:11	59
1/5/2017 0:51	58	2/5/2017 1:56	55	3/5/2017 3:01	56	4/5/2017 4:06	54	5/5/2017 5:11	58	6/5/2017 6:16	59
1/5/2017 0:56	57	2/5/2017 2:01	55	3/5/2017 3:06	57	4/5/2017 4:11	55	5/5/2017 5:16	58	6/5/2017 6:21	58
1/5/2017 1:01	58	2/5/2017 2:06	55	3/5/2017 3:11	57	4/5/2017 4:16	55	5/5/2017 5:21	59	6/5/2017 6:26	59
1/5/2017 1:06	56	2/5/2017 2:11	55	3/5/2017 3:16	58	4/5/2017 4:21	54	5/5/2017 5:26	59	6/5/2017 6:31	59
1/5/2017 1:11	57	2/5/2017 2:16	55	3/5/2017 3:21	56	4/5/2017 4:26	54	5/5/2017 5:31	59	6/5/2017 6:36	60
1/5/2017 1:16	57	2/5/2017 2:21	55	3/5/2017 3:26	55	4/5/2017 4:31	56	5/5/2017 5:36	59	6/5/2017 6:41	60
1/5/2017 1:21	57	2/5/2017 2:26	55	3/5/2017 3:31	55	4/5/2017 4:36	55	5/5/2017 5:41	59	6/5/2017 6:46	59
1/5/2017 1:26	57	2/5/2017 2:31	55	3/5/2017 3:36	56	4/5/2017 4:41	54	5/5/2017 5:46	60	6/5/2017 6:51	61
1/5/2017 1:31	56	2/5/2017 2:36	54	3/5/2017 3:41	56	4/5/2017 4:46	55	5/5/2017 5:51	60	6/5/2017 6:56	60
1/5/2017 1:36	58	2/5/2017 2:41	54	3/5/2017 3:46	56	4/5/2017 4:51	55	5/5/2017 5:56	60	6/5/2017 7:01	59
1/5/2017 1:41	58	2/5/2017 2:46	54	3/5/2017 3:51	55	4/5/2017 4:56	54	5/5/2017 6:01	60	6/5/2017 7:06	59
1/5/2017 1:46	56	2/5/2017 2:51	56	3/5/2017 3:56	56	4/5/2017 5:01	58	5/5/2017 6:06	61	6/5/2017 7:11	60
1/5/2017 1:51	57	2/5/2017 2:56	54	3/5/2017 4:01	56	4/5/2017 5:06	56	5/5/2017 6:11	61	6/5/2017 7:16	59
1/5/2017 1:56	55	2/5/2017 3:01	53	3/5/2017 4:06	55	4/5/2017 5:11	55	5/5/2017 6:16	48	6/5/2017 7:21	59
1/5/2017 2:01	56	2/5/2017 3:06	54	3/5/2017 4:11	54	4/5/2017 5:16	55	5/5/2017 6:21	44	6/5/2017 7:26	58
1/5/2017 2:06	57	2/5/2017 3:11	54	3/5/2017 4:16	55	4/5/2017 5:21	56	5/5/2017 6:26	51	6/5/2017 7:31	59
1/5/2017 2:11	56	2/5/2017 3:16	54	3/5/2017 4:21	55	4/5/2017 5:26	55	5/5/2017 6:31	51	6/5/2017 7:36	60
1/5/2017 2:16	57	2/5/2017 3:21	54	3/5/2017 4:26	56	4/5/2017 5:31	56	5/5/2017 6:36	55	6/5/2017 7:41	59
1/5/2017 2:21	56	2/5/2017 3:26	55	3/5/2017 4:31	57	4/5/2017 5:36	58	5/5/2017 6:41	57	6/5/2017 7:46	58
1/5/2017 2:26	57	2/5/2017 3:31	55	3/5/2017 4:36	55	4/5/2017 5:41	57	5/5/2017 6:46	56	6/5/2017 7:51	60
1/5/2017 2:31	56	2/5/2017 3:36	55	3/5/2017 4:41	56	4/5/2017 5:46	56	5/5/2017 6:51	55	6/5/2017 7:56	59
1/5/2017 2:36	56	2/5/2017 3:41	54	3/5/2017 4:46	57	4/5/2017 5:51	58	5/5/2017 6:56	56	7/5/2017 0:01	58
1/5/2017 2:41	55	2/5/2017 3:46	53	3/5/2017 4:51	59	4/5/2017 5:56	57	5/5/2017 7:01	60	7/5/2017 0:06	58
1/5/2017 2:46	55	2/5/2017 3:51	55	3/5/2017 4:56	57	4/5/2017 6:01	58	5/5/2017 7:06	61	7/5/2017 0:11	58
1/5/2017 2:51	55	2/5/2017 3:56	53	3/5/2017 5:01	56	4/5/2017 6:06	58	5/5/2017 7:11	59	7/5/2017 0:16	58
1/5/2017 2:56	56	2/5/2017 4:01	54	3/5/2017 5:06	57	4/5/2017 6:11	58	5/5/2017 7:16	59	7/5/2017 0:21	58
1/5/2017 3:01	55	2/5/2017 4:06	54	3/5/2017 5:11	57	4/5/2017 6:16	58	5/5/2017 7:21	60	7/5/2017 0:26	58
1/5/2017 3:06	56	2/5/2017 4:11	55	3/5/2017 5:16	56	4/5/2017 6:21	59	5/5/2017 7:26	60	7/5/2017 0:31	59
1/5/2017 3:11	56	2/5/2017 4:16	54	3/5/2017 5:21	58	4/5/2017 6:26	60	5/5/2017 7:31	59	7/5/2017 0:36	58
1/5/2017 3:16	55	2/5/2017 4:21	55	3/5/2017 5:26	58	4/5/2017 6:31	51	5/5/2017 7:36	59	7/5/2017 0:41	57
1/5/2017 3:21	55	2/5/2017 4:26	55	3/5/2017 5:31	59	4/5/2017 6:36	60	5/5/2017 7:41	58	7/5/2017 0:46	57
1/5/2017 3:26	55	2/5/2017 4:31	55	3/5/2017 5:36	57	4/5/2017 6:41	51	5/5/2017 7:46	59	7/5/2017 0:51	57
1/5/2017 3:31	55	2/5/2017 4:36	54	3/5/2017 5:41	57	4/5/2017 6:46	52	5/5/2017 7:51	59	7/5/2017 0:56	57
1/5/2017 3:36	54	2/5/2017 4:41	55	3/5/2017 5:46	58	4/5/2017 6:51	61	5/5/2017 7:56	60	7/5/2017 1:01	57
1/5/2017 3:41	55	2/5/2017 4:46	54	3/5/2017 5:51	57	4/5/2017 6:56	61	6/5/2017 0:01	60	7/5/2017 1:06	56
1/5/2017 3:46	55	2/5/2017 4:51	54	3/5/2017 5:56	58	4/5/2017 7:01	61	6/5/2017 0:06	59	7/5/2017 1:11	57
1/5/2017 3:51	54	2/5/2017 4:56	56	3/5/2017 6:01	57	4/5/2017 7:06	61	6/5/2017 0:11	60	7/5/2017 1:16	57
1/5/2017 3:56	55	2/5/2017 5:01	55	3/5/2017 6:06	58	4/5/2017 7:11	60	6/5/2017 0:16	58	7/5/2017 1:21	57
1/5/2017 4:01	55	2/5/2017 5:06	56	3/5/2017 6:11	57	4/5/2017 7:16	61	6/5/2017 0:21	59	7/5/2017 1:26	58
1/5/2017 4:06	55	2/5/2017 5:11	56	3/5/2017 6:16	58	4/5/2017 7:21	60	6/5/2017 0:26	59	7/5/2017 1:31	57
1/5/2017 4:11	54	2/5/2017 5:16	57	3/5/2017 6:21	58	4/5/2017 7:26	39	6/5/2017 0:31	58	7/5/2017 1:36	57
1/5/2017 4:16	55	2/5/2017 5:21	56	3/5/2017 6:26	59	4/5/2017 7:31	61	6/5/2017 0:36	59	7/5/2017 1:41	61
1/5/2017 4:21	54	2/5/2017 5:26	56	3/5/2017 6:31	58	4/5/2017 7:36	60	6/5/2017 0:41	58	7/5/2017 1:46	58
1/5/2017 4:26	57	2/5/2017 5:31	58	3/5/2017 6:36	60	4/5/2017 7:41	61	6/5/2017 0:46	58	7/5/2017 1:51	58
1/5/2017 4:31	55	2/5/2017 5:36	58	3/5/2017 6:41	59	4/5/2017 7:46	60	6/5/2017 0:51	58	7/5/2017 1:56	59
1/5/2017 4:36	57	2/5/2017 5:41	57	3/5/2017 6:46	59	4/5/2017 7:51	60	6/5/2017 0:56	58	7/5/2017 2:01	60
1/5/2017 4:41	54	2/5/2017 5:46	57	3/5/2017 6:51	59	4/5/2017 7:56	60	6/5/2017 1:01	58	7/5/2017 2:06	60
1/5/2017 4:46	58	2/5/2017 5:51	57	3/5/2017 6:56	58	5/5/2017 0:01	61	6/5/2017 1:06	58	7/5/2017 2:11	60
1/5/2017 4:51	55	2/5/2017 5:56	57	3/5/2017 7:01	58	5/5/2017 0:06	60	6/5/2017 1:11	58	7/5/2017 2:16	60
1/5/2017 4:56	55	2/5/2017 6:01	58	3/5/2017 7:06	59	5/5/2017 0:11	60	6/5/2017 1:16	59	7/5/2017 2:21	60
1/5/2017 5:01	56	2/5/2017 6:06	58	3/5/2017 7:11	59	5/5/2017 0:16	60	6/5/2017 1:21	58	7/5/2017 2:26	60
1/5/2017 5:06	56	2/5/2017 6:11	57	3/5/2017 7:16	58	5/5/2017 0:21	60	6/5/2017 1:26	58	7/5/2017 2:31	60
1/5/2017 5:11	57	2/5/2017 6:16	59	3/5/2017 7:21	59	5/5/2017 0:26	60	6/5/2017 1:31	57	7/5/2017 2:36	60
1/5/2017 5:16	57	2/5/2017 6:21	59	3/5/2017 7:26	58	5/5/2017 0:31	59	6/5/2017 1:36	57	7/5/2017 2:41	61
1/5/2017 5:21	57	2/5/2017 6:26	60	3/5/2017 7:31	58	5/5/2017 0:36	60	6/5/2017 1:41	58	7/5/2017 2:46	61
1/5/2017 5:26	56	2/5/2017 6:31	60	3/5/2017 7:36	58	5/5/2017 0:41	61	6/5/2017 1:46	58	7/5/2017 2:51	61
1/5/2017 5:31	57	2/5/2017 6:36	60	3/5/2017 7:41	58	5/5/2017 0:46	60	6/5/2017 1:51	59	7/5/2017 2:56	47
1/5/2017 5:36	57	2/5/2017 6:41	60	3/5/2017 7:46	58	5/5/2017 0:51	59	6/5/2017 1:56	57	7/5/2017 3:01	48
1/5/2017 5:41	59	2/5/2017 6:46	49	3/5/2017 7:51	58	5/5/2017 0:56	59	6/5/2017 2:01	57	7/5/2017 3:06	56
1/5/2017 5:46	56	2/5/2017 6:51	60	3/5/2017 7:56	57	5/5/2017 1:01	60	6/5/2017 2:06	57	7/5/2017 3:11	56
1/5/2017 5:51	58	2/5/2017 6:56	60	4/5/2017 0:01	57	5/5/2017 1:06	60	6/5/2017 2:11	57	7/5/2017 3:16	55
1/5/2017 5:56	57	2/5/2017 7:01	59	4/5/2017 0:06	57	5/5/2017 1:11	59	6/5/2017 2:16	58	7/5/2017 3:21	54
1/5/2017 6:01	57	2/5/2017 7:06	59	4/5/2017 0:11	57	5/5/2017 1:16	59	6/5/2017 2:21	56	7/5/2017 3:26	53
1/5/2017 6:06	58	2/5/2017 7:11	59	4/5/2017 0:16	57	5/5/2017 1:21	59	6/5/2017 2:26	57	7/5/2017 3:31	55
1/5/2017 6:11	57	2/5/2017 7:16	59	4/5/2017 0:21	57	5/5/2017 1:26	59	6/5/2017 2:31	57	7/5/2017 3:36	55
1/5/2017 6:16	58	2/5/2017 7:21	59	4/5/2017 0:26	57	5/5/2017 1:31	60	6/5/2017 2:36	57	7	


Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
7/5/2017 6:16	61	8/5/2017 23:21	47	10/5/2017 0:26	58	11/5/2017 1:31	59	12/5/2017 2:36	56	13/5/2017 3:41	56
7/5/2017 6:21	61	8/5/2017 23:26	60	10/5/2017 0:31	59	11/5/2017 1:36	59	12/5/2017 2:41	55	13/5/2017 3:46	57
7/5/2017 6:26	61	8/5/2017 23:31	60	10/5/2017 0:36	58	11/5/2017 1:41	59	12/5/2017 2:46	55	13/5/2017 3:51	57
7/5/2017 6:31	45	8/5/2017 23:36	60	10/5/2017 0:41	58	11/5/2017 1:46	58	12/5/2017 2:51	55	13/5/2017 3:56	58
7/5/2017 6:36	46	8/5/2017 23:41	59	10/5/2017 0:46	58	11/5/2017 1:51	59	12/5/2017 2:56	55	13/5/2017 4:01	56
7/5/2017 6:41	61	8/5/2017 23:46	59	10/5/2017 0:51	59	11/5/2017 1:56	58	12/5/2017 3:01	56	13/5/2017 4:06	57
7/5/2017 6:46	50	8/5/2017 23:51	59	10/5/2017 0:56	59	11/5/2017 2:01	58	12/5/2017 3:06	55	13/5/2017 4:11	56
7/5/2017 6:51	61	8/5/2017 23:56	59	10/5/2017 1:01	58	11/5/2017 2:06	59	12/5/2017 3:11	56	13/5/2017 4:16	56
7/5/2017 6:56	60	9/5/2017 0:01	59	10/5/2017 1:06	58	11/5/2017 2:11	59	12/5/2017 3:16	58	13/5/2017 4:21	56
7/5/2017 23:01	45	9/5/2017 0:06	58	10/5/2017 1:11	57	11/5/2017 2:16	58	12/5/2017 3:21	55	13/5/2017 4:26	57
7/5/2017 23:06	49	9/5/2017 0:11	59	10/5/2017 1:16	58	11/5/2017 2:21	58	12/5/2017 3:26	55	13/5/2017 4:31	58
7/5/2017 23:11	46	9/5/2017 0:16	58	10/5/2017 1:21	57	11/5/2017 2:26	58	12/5/2017 3:31	55	13/5/2017 4:36	58
7/5/2017 23:16	60	9/5/2017 0:21	58	10/5/2017 1:26	57	11/5/2017 2:31	58	12/5/2017 3:36	55	13/5/2017 4:41	57
7/5/2017 23:21	60	9/5/2017 0:26	58	10/5/2017 1:31	57	11/5/2017 2:36	59	12/5/2017 3:41	55	13/5/2017 4:46	56
7/5/2017 23:26	60	9/5/2017 0:31	58	10/5/2017 1:36	58	11/5/2017 2:41	59	12/5/2017 3:46	54	13/5/2017 4:51	57
7/5/2017 23:31	60	9/5/2017 0:36	58	10/5/2017 1:41	57	11/5/2017 2:46	47	12/5/2017 3:51	55	13/5/2017 4:56	57
7/5/2017 23:36	60	9/5/2017 0:41	58	10/5/2017 1:46	57	11/5/2017 2:51	58	12/5/2017 3:56	54	13/5/2017 5:01	57
7/5/2017 23:41	60	9/5/2017 0:46	57	10/5/2017 1:51	57	11/5/2017 2:56	58	12/5/2017 4:01	55	13/5/2017 5:06	57
7/5/2017 23:46	60	9/5/2017 0:51	57	10/5/2017 1:56	57	11/5/2017 3:01	58	12/5/2017 4:06	56	13/5/2017 5:11	58
7/5/2017 23:51	38	9/5/2017 0:56	57	10/5/2017 2:01	58	11/5/2017 3:06	58	12/5/2017 4:11	54	13/5/2017 5:16	58
7/5/2017 23:56	50	9/5/2017 1:01	57	10/5/2017 2:06	57	11/5/2017 3:11	57	12/5/2017 4:16	55	13/5/2017 5:21	58
8/5/2017 0:01	35	9/5/2017 1:06	58	10/5/2017 2:11	56	11/5/2017 3:16	58	12/5/2017 4:21	54	13/5/2017 5:26	58
8/5/2017 0:06	53	9/5/2017 1:11	57	10/5/2017 2:16	57	11/5/2017 3:21	58	12/5/2017 4:26	55	13/5/2017 5:31	59
8/5/2017 0:11	61	9/5/2017 1:16	58	10/5/2017 2:21	57	11/5/2017 3:26	58	12/5/2017 4:31	59	13/5/2017 5:36	59
8/5/2017 0:16	41	9/5/2017 1:21	60	10/5/2017 2:26	57	11/5/2017 3:31	58	12/5/2017 4:36	55	13/5/2017 5:41	58
8/5/2017 0:21	61	9/5/2017 1:26	60	10/5/2017 2:31	56	11/5/2017 3:36	58	12/5/2017 4:41	55	13/5/2017 5:46	58
8/5/2017 0:26	55	9/5/2017 1:31	59	10/5/2017 2:36	55	11/5/2017 3:41	58	12/5/2017 4:46	54	13/5/2017 5:51	59
8/5/2017 0:31	50	9/5/2017 1:36	59	10/5/2017 2:41	56	11/5/2017 3:46	57	12/5/2017 4:51	55	13/5/2017 5:56	59
8/5/2017 0:36	49	9/5/2017 1:41	59	10/5/2017 2:46	56	11/5/2017 3:51	57	12/5/2017 4:56	55	13/5/2017 6:01	58
8/5/2017 0:41	61	9/5/2017 1:46	59	10/5/2017 2:51	57	11/5/2017 3:56	58	12/5/2017 5:01	56	13/5/2017 6:06	59
8/5/2017 0:46	61	9/5/2017 1:51	59	10/5/2017 2:56	56	11/5/2017 4:01	58	12/5/2017 5:06	55	13/5/2017 6:11	59
8/5/2017 0:51	61	9/5/2017 1:56	59	10/5/2017 3:01	56	11/5/2017 4:06	59	12/5/2017 5:11	55	13/5/2017 6:16	60
8/5/2017 0:56	61	9/5/2017 2:01	61	10/5/2017 3:06	56	11/5/2017 4:11	58	12/5/2017 5:16	56	13/5/2017 6:21	59
8/5/2017 1:01	60	9/5/2017 2:06	55	10/5/2017 3:11	57	11/5/2017 4:16	58	12/5/2017 5:21	56	13/5/2017 6:26	59
8/5/2017 1:06	61	9/5/2017 2:11	55	10/5/2017 3:16	57	11/5/2017 4:21	58	12/5/2017 5:26	57	13/5/2017 6:31	59
8/5/2017 1:11	60	9/5/2017 2:16	49	10/5/2017 3:21	56	11/5/2017 4:26	58	12/5/2017 5:31	57	13/5/2017 6:36	60
8/5/2017 1:16	61	9/5/2017 2:21	61	10/5/2017 3:26	56	11/5/2017 4:31	58	12/5/2017 5:36	58	13/5/2017 6:41	61
8/5/2017 1:21	61	9/5/2017 2:26	61	10/5/2017 3:31	56	11/5/2017 4:36	59	12/5/2017 5:41	57	13/5/2017 6:46	60
8/5/2017 1:26	60	9/5/2017 2:31	61	10/5/2017 3:36	56	11/5/2017 4:41	58	12/5/2017 5:46	56	13/5/2017 6:51	60
8/5/2017 1:31	60	9/5/2017 2:36	60	10/5/2017 3:41	57	11/5/2017 4:46	58	12/5/2017 5:51	58	13/5/2017 6:56	60
8/5/2017 1:36	60	9/5/2017 2:41	60	10/5/2017 3:46	56	11/5/2017 4:51	58	12/5/2017 5:56	57	13/5/2017 23:01	60
8/5/2017 1:41	60	9/5/2017 2:46	60	10/5/2017 3:51	57	11/5/2017 4:56	59	12/5/2017 6:01	57	13/5/2017 23:06	60
8/5/2017 1:46	60	9/5/2017 2:51	61	10/5/2017 3:56	56	11/5/2017 5:01	58	12/5/2017 6:06	57	13/5/2017 23:11	59
8/5/2017 1:51	60	9/5/2017 2:56	55	10/5/2017 4:01	56	11/5/2017 5:06	58	12/5/2017 6:11	59	13/5/2017 23:16	59
8/5/2017 1:56	60	9/5/2017 3:01	61	10/5/2017 4:06	56	11/5/2017 5:11	58	12/5/2017 6:16	58	13/5/2017 23:21	59
8/5/2017 2:01	60	9/5/2017 3:06	60	10/5/2017 4:11	57	11/5/2017 5:16	58	12/5/2017 6:21	59	13/5/2017 23:26	59
8/5/2017 2:06	60	9/5/2017 3:11	60	10/5/2017 4:16	57	11/5/2017 5:21	58	12/5/2017 6:26	60	13/5/2017 23:31	59
8/5/2017 2:11	60	9/5/2017 3:16	58	10/5/2017 4:21	56	11/5/2017 5:26	58	12/5/2017 6:31	60	13/5/2017 23:36	59
8/5/2017 2:16	60	9/5/2017 3:21	58	10/5/2017 4:26	57	11/5/2017 5:31	59	12/5/2017 6:36	61	13/5/2017 23:41	59
8/5/2017 2:21	60	9/5/2017 3:26	58	10/5/2017 4:31	57	11/5/2017 5:36	59	12/5/2017 6:41	55	13/5/2017 23:46	59
8/5/2017 2:26	60	9/5/2017 3:31	58	10/5/2017 4:36	57	11/5/2017 5:41	59	12/5/2017 6:46	60	13/5/2017 23:51	58
8/5/2017 2:31	60	9/5/2017 3:36	57	10/5/2017 4:41	57	11/5/2017 5:46	59	12/5/2017 6:51	61	13/5/2017 23:56	58
8/5/2017 2:36	59	9/5/2017 3:41	57	10/5/2017 4:46	57	11/5/2017 5:51	60	12/5/2017 6:56	52	14/5/2017 0:01	59
8/5/2017 2:41	58	9/5/2017 3:46	57	10/5/2017 4:51	58	11/5/2017 5:56	59	12/5/2017 23:01	38	14/5/2017 0:06	59
8/5/2017 2:46	56	9/5/2017 3:51	57	10/5/2017 4:56	57	11/5/2017 6:01	59	12/5/2017 23:06	60	14/5/2017 0:11	59
8/5/2017 2:51	55	9/5/2017 3:56	57	10/5/2017 5:01	57	11/5/2017 6:06	60	12/5/2017 23:11	60	14/5/2017 0:16	59
8/5/2017 2:56	54	9/5/2017 4:01	56	10/5/2017 5:06	57	11/5/2017 6:11	60	12/5/2017 23:16	60	14/5/2017 0:21	59
8/5/2017 3:01	55	9/5/2017 4:06	55	10/5/2017 5:11	57	11/5/2017 6:16	60	12/5/2017 23:21	61	14/5/2017 0:26	59
8/5/2017 3:06	55	9/5/2017 4:11	55	10/5/2017 5:16	57	11/5/2017 6:21	61	12/5/2017 23:26	60	14/5/2017 0:31	60
8/5/2017 3:11	54	9/5/2017 4:16	55	10/5/2017 5:21	58	11/5/2017 6:26	50	12/5/2017 23:31	60	14/5/2017 0:36	58
8/5/2017 3:16	53	9/5/2017 4:21	57	10/5/2017 5:26	58	11/5/2017 6:31	61	12/5/2017 23:36	60	14/5/2017 0:41	58
8/5/2017 3:21	54	9/5/2017 4:26	57	10/5/2017 5:31	59	11/5/2017 6:36	53	12/5/2017 23:41	61	14/5/2017 0:46	59
8/5/2017 3:26	54	9/5/2017 4:31	56	10/5/2017 5:36	60	11/5/2017 6:41	54	12/5/2017 23:46	49	14/5/2017 0:51	58
8/5/2017 3:31	56	9/5/2017 4:36	56	10/5/2017 5:41	58	11/5/2017 6:46	51	12/5/2017 23:51	59	14/5/2017 0:56	58
8/5/2017 3:36	56	9/5/2017 4:41	56	10/5/2017 5:46	60	11/5/2017 6:51	52	12/5/2017 23:56	59	14/5/2017 1:01	59
8/5/2017 3:41	54	9/5/2017 4:46	56	10/5/2017 5:51	59	11/5/2017 6:56	61	13/5/2017 0:01	60	14/5/2017 1:06	58
8/5/2017 3:46	54	9/5/2017 4:51	56	10/5/2017 5:56	59	11/5/2017 23:01	59	13/5/2017 0:06	59	14/5/2017 1:11	59
8/5/2017 3:51	55	9/5/2017 4:56	57	10/5/2017 6:01	59	11/5/2017 23:06	59	13/5/2017 0:11	59	14/5/2017 1:16	57
8/5/2017 3:56	55	9/5/2017 5:01	56	10/5/2017 6:06	60	11/5/2017 23:11	59	13/5/2017 0:16	60	14/5/2017 1:21	58
8/5/2017 4:01	55	9/5/2017 5:06	57	10/5/2017 6:11	60	11/5/2017 23:16	59	13/5/2017 0:21	61	14/5/2017 1:26	58
8/5/2017 4:06	55	9/5/2017 5:11	56	10/5/2017 6:16	61	11/5/2017 23:21	58	13/5/2017 0:26	60	14/5/2017 1:31	58
8/5/2017 4:11	55	9/5/2017 5:16	57	10/5/2017 6:21	60	11/5/2017 23:26	59	13/5/2017 0:31	59	14/5/2017 1:36	59
8/5/2017 4:16	54	9/5/2017 5:21	57	10/5/2017 6:26	49	11/5/2017 23:31	59	13/5/2017 0:36	60	14/5/2017 1:41	58
8/5/2017 4:21	55	9/5/2017 5:26	57	10/5/2017 6:31	61	11/5/2017 23:36	59	13/5/2017 0:41	59	14/5/2017 1:46	58
8/5/2017 4:26	55	9/5/2017 5:31	57	10/5/2017 6:36	53	11/5/2017 23:41	59	13/5/2017 0:46	59	14/5/2017 1:51	58
8/5/2017 4:31	55	9/5/2017 5:36	58	10/5/2017 6:41	51	11/5/2017 23:46	58	13/5/2017 0:51	59	14/5/2017 1:56	56
8/5/2017 4:36	55	9/5/2017 5:41	58	10/5/2017 6:46	61	11/5/20					

Real-time Noise Data		RTN4 (Causeway Bay Community Centre)									
14/5/2017 4:46	56	15/5/2017 5:51	58	16/5/2017 6:56	61	18/5/2017 0:01	59	19/5/2017 1:06	58	20/5/2017 2:11	56
14/5/2017 4:51	57	15/5/2017 5:56	58	16/5/2017 23:01	60	18/5/2017 0:06	59	19/5/2017 1:11	58	20/5/2017 2:16	56
14/5/2017 4:56	57	15/5/2017 6:01	59	16/5/2017 23:06	59	18/5/2017 0:11	59	19/5/2017 1:16	57	20/5/2017 2:21	56
14/5/2017 5:01	56	15/5/2017 6:06	60	16/5/2017 23:11	59	18/5/2017 0:16	58	19/5/2017 1:21	57	20/5/2017 2:26	56
14/5/2017 5:06	57	15/5/2017 6:11	59	16/5/2017 23:16	59	18/5/2017 0:21	58	19/5/2017 1:26	57	20/5/2017 2:31	56
14/5/2017 5:11	57	15/5/2017 6:16	60	16/5/2017 23:21	59	18/5/2017 0:26	59	19/5/2017 1:31	57	20/5/2017 2:36	56
14/5/2017 5:16	57	15/5/2017 6:21	59	16/5/2017 23:26	59	18/5/2017 0:31	58	19/5/2017 1:36	59	20/5/2017 2:41	56
14/5/2017 5:21	57	15/5/2017 6:26	60	16/5/2017 23:31	59	18/5/2017 0:36	57	19/5/2017 1:41	56	20/5/2017 2:46	56
14/5/2017 5:26	59	15/5/2017 6:31	61	16/5/2017 23:36	59	18/5/2017 0:41	58	19/5/2017 1:46	57	20/5/2017 2:51	56
14/5/2017 5:31	59	15/5/2017 6:36	35	16/5/2017 23:41	59	18/5/2017 0:46	59	19/5/2017 1:51	57	20/5/2017 2:56	56
14/5/2017 5:36	58	15/5/2017 6:41	49	16/5/2017 23:46	58	18/5/2017 0:51	58	19/5/2017 1:56	57	20/5/2017 3:01	56
14/5/2017 5:41	59	15/5/2017 6:46	53	16/5/2017 23:51	58	18/5/2017 0:56	57	19/5/2017 2:01	56	20/5/2017 3:06	56
14/5/2017 5:46	59	15/5/2017 6:51	61	16/5/2017 23:56	59	18/5/2017 1:01	58	19/5/2017 2:06	57	20/5/2017 3:11	55
14/5/2017 5:51	58	15/5/2017 6:56	60	17/5/2017 0:01	59	18/5/2017 1:06	58	19/5/2017 2:11	56	20/5/2017 3:16	56
14/5/2017 5:56	58	15/5/2017 23:01	60	17/5/2017 0:06	58	18/5/2017 1:11	57	19/5/2017 2:16	55	20/5/2017 3:21	55
14/5/2017 6:01	58	15/5/2017 23:06	59	17/5/2017 0:11	58	18/5/2017 1:16	57	19/5/2017 2:21	56	20/5/2017 3:26	56
14/5/2017 6:06	58	15/5/2017 23:11	59	17/5/2017 0:16	58	18/5/2017 1:21	58	19/5/2017 2:26	56	20/5/2017 3:31	55
14/5/2017 6:11	58	15/5/2017 23:16	58	17/5/2017 0:21	59	18/5/2017 1:26	58	19/5/2017 2:31	56	20/5/2017 3:36	55
14/5/2017 6:16	59	15/5/2017 23:21	59	17/5/2017 0:26	59	18/5/2017 1:31	59	19/5/2017 2:36	56	20/5/2017 3:41	55
14/5/2017 6:21	59	15/5/2017 23:26	59	17/5/2017 0:31	59	18/5/2017 1:36	56	19/5/2017 2:41	55	20/5/2017 3:46	57
14/5/2017 6:26	60	15/5/2017 23:31	59	17/5/2017 0:36	57	18/5/2017 1:41	56	19/5/2017 2:46	55	20/5/2017 3:51	55
14/5/2017 6:31	60	15/5/2017 23:36	58	17/5/2017 0:41	58	18/5/2017 1:46	57	19/5/2017 2:51	55	20/5/2017 3:56	55
14/5/2017 6:36	59	15/5/2017 23:41	58	17/5/2017 0:46	58	18/5/2017 1:51	57	19/5/2017 2:56	56	20/5/2017 4:01	55
14/5/2017 6:41	59	15/5/2017 23:46	59	17/5/2017 0:51	59	18/5/2017 1:56	55	19/5/2017 3:01	55	20/5/2017 4:06	55
14/5/2017 6:46	59	15/5/2017 23:51	58	17/5/2017 0:56	58	18/5/2017 2:01	57	19/5/2017 3:06	56	20/5/2017 4:11	55
14/5/2017 6:51	59	15/5/2017 23:56	58	17/5/2017 1:01	59	18/5/2017 2:06	56	19/5/2017 3:11	55	20/5/2017 4:16	56
14/5/2017 6:56	58	16/5/2017 0:01	58	17/5/2017 1:06	58	18/5/2017 2:11	56	19/5/2017 3:16	55	20/5/2017 4:21	56
14/5/2017 23:01	59	16/5/2017 0:06	58	17/5/2017 1:11	57	18/5/2017 2:16	56	19/5/2017 3:21	55	20/5/2017 4:26	56
14/5/2017 23:06	60	16/5/2017 0:11	57	17/5/2017 1:16	58	18/5/2017 2:21	58	19/5/2017 3:26	55	20/5/2017 4:31	54
14/5/2017 23:11	60	16/5/2017 0:16	58	17/5/2017 1:21	55	18/5/2017 2:26	57	19/5/2017 3:31	56	20/5/2017 4:36	55
14/5/2017 23:16	61	16/5/2017 0:21	57	17/5/2017 1:26	50	18/5/2017 2:31	57	19/5/2017 3:36	56	20/5/2017 4:41	56
14/5/2017 23:21	60	16/5/2017 0:26	58	17/5/2017 1:31	59	18/5/2017 2:36	55	19/5/2017 3:41	56	20/5/2017 4:46	55
14/5/2017 23:26	60	16/5/2017 0:31	57	17/5/2017 1:36	53	18/5/2017 2:41	55	19/5/2017 3:46	55	20/5/2017 4:51	55
14/5/2017 23:31	60	16/5/2017 0:36	56	17/5/2017 1:41	59	18/5/2017 2:46	55	19/5/2017 3:51	54	20/5/2017 4:56	55
14/5/2017 23:36	60	16/5/2017 0:41	57	17/5/2017 1:46	59	18/5/2017 2:51	57	19/5/2017 3:56	54	20/5/2017 5:01	56
14/5/2017 23:41	59	16/5/2017 0:46	57	17/5/2017 1:51	59	18/5/2017 2:56	55	19/5/2017 4:01	55	20/5/2017 5:06	56
14/5/2017 23:46	59	16/5/2017 0:51	53	17/5/2017 1:56	57	18/5/2017 3:01	55	19/5/2017 4:06	55	20/5/2017 5:11	56
14/5/2017 23:51	60	16/5/2017 0:56	59	17/5/2017 2:01	57	18/5/2017 3:06	56	19/5/2017 4:11	54	20/5/2017 5:16	56
14/5/2017 23:56	60	16/5/2017 1:01	60	17/5/2017 2:06	57	18/5/2017 3:11	56	19/5/2017 4:16	54	20/5/2017 5:21	56
15/5/2017 0:01	59	16/5/2017 1:06	60	17/5/2017 2:11	57	18/5/2017 3:16	56	19/5/2017 4:21	55	20/5/2017 5:26	56
15/5/2017 0:06	59	16/5/2017 1:11	61	17/5/2017 2:16	57	18/5/2017 3:21	54	19/5/2017 4:26	55	20/5/2017 5:31	56
15/5/2017 0:11	60	16/5/2017 1:16	60	17/5/2017 2:21	56	18/5/2017 3:26	55	19/5/2017 4:31	54	20/5/2017 5:36	57
15/5/2017 0:16	59	16/5/2017 1:21	58	17/5/2017 2:26	58	18/5/2017 3:31	55	19/5/2017 4:36	56	20/5/2017 5:41	56
15/5/2017 0:21	59	16/5/2017 1:26	60	17/5/2017 2:31	57	18/5/2017 3:36	56	19/5/2017 4:41	55	20/5/2017 5:46	57
15/5/2017 0:26	59	16/5/2017 1:31	52	17/5/2017 2:36	56	18/5/2017 3:41	60	19/5/2017 4:46	55	20/5/2017 5:51	57
15/5/2017 0:31	60	16/5/2017 1:36	60	17/5/2017 2:41	56	18/5/2017 3:46	56	19/5/2017 4:51	55	20/5/2017 5:56	57
15/5/2017 0:36	58	16/5/2017 1:41	58	17/5/2017 2:46	56	18/5/2017 3:51	56	19/5/2017 4:56	57	20/5/2017 6:01	57
15/5/2017 0:41	59	16/5/2017 1:46	57	17/5/2017 2:51	57	18/5/2017 3:56	56	19/5/2017 5:01	56	20/5/2017 6:06	58
15/5/2017 0:46	58	16/5/2017 1:51	57	17/5/2017 2:56	57	18/5/2017 4:01	55	19/5/2017 5:06	57	20/5/2017 6:11	57
15/5/2017 0:51	59	16/5/2017 1:56	57	17/5/2017 3:01	57	18/5/2017 4:06	56	19/5/2017 5:11	55	20/5/2017 6:16	58
15/5/2017 0:56	59	16/5/2017 2:01	57	17/5/2017 3:06	57	18/5/2017 4:11	55	19/5/2017 5:16	55	20/5/2017 6:21	58
15/5/2017 1:01	58	16/5/2017 2:06	57	17/5/2017 3:11	55	18/5/2017 4:16	55	19/5/2017 5:21	57	20/5/2017 6:26	59
15/5/2017 1:06	58	16/5/2017 2:11	56	17/5/2017 3:16	56	18/5/2017 4:21	55	19/5/2017 5:26	59	20/5/2017 6:31	59
15/5/2017 1:11	59	16/5/2017 2:16	56	17/5/2017 3:21	56	18/5/2017 4:26	57	19/5/2017 5:31	59	20/5/2017 6:36	59
15/5/2017 1:16	59	16/5/2017 2:21	57	17/5/2017 3:26	55	18/5/2017 4:31	57	19/5/2017 5:36	58	20/5/2017 6:41	60
15/5/2017 1:21	60	16/5/2017 2:26	55	17/5/2017 3:31	56	18/5/2017 4:36	57	19/5/2017 5:41	57	20/5/2017 6:46	60
15/5/2017 1:26	58	16/5/2017 2:31	56	17/5/2017 3:36	57	18/5/2017 4:41	55	19/5/2017 5:46	57	20/5/2017 6:51	60
15/5/2017 1:31	58	16/5/2017 2:36	55	17/5/2017 3:41	56	18/5/2017 4:46	56	19/5/2017 5:51	57	20/5/2017 6:56	59
15/5/2017 1:36	58	16/5/2017 2:41	56	17/5/2017 3:46	56	18/5/2017 4:51	56	19/5/2017 5:56	59	20/5/2017 23:01	56
15/5/2017 1:41	58	16/5/2017 2:46	55	17/5/2017 3:51	56	18/5/2017 4:56	56	19/5/2017 6:01	57	20/5/2017 23:06	53
15/5/2017 1:46	57	16/5/2017 2:51	54	17/5/2017 3:56	56	18/5/2017 5:01	55	19/5/2017 6:06	57	20/5/2017 23:11	55
15/5/2017 1:51	59	16/5/2017 2:56	56	17/5/2017 4:01	56	18/5/2017 5:06	57	19/5/2017 6:11	58	20/5/2017 23:16	55
15/5/2017 1:56	59	16/5/2017 3:01	56	17/5/2017 4:06	56	18/5/2017 5:11	57	19/5/2017 6:16	60	20/5/2017 23:21	55
15/5/2017 2:01	59	16/5/2017 3:06	54	17/5/2017 4:11	56	18/5/2017 5:16	57	19/5/2017 6:21	59	20/5/2017 23:26	53
15/5/2017 2:06	57	16/5/2017 3:11	55	17/5/2017 4:16	57	18/5/2017 5:21	57	19/5/2017 6:26	60	20/5/2017 23:31	55
15/5/2017 2:11	57	16/5/2017 3:16	56	17/5/2017 4:21	56	18/5/2017 5:26	59	19/5/2017 6:31	60	20/5/2017 23:36	54
15/5/2017 2:16	58	16/5/2017 3:21	55	17/5/2017 4:26	57	18/5/2017 5:31	58	19/5/2017 6:36	60	20/5/2017 23:41	54
15/5/2017 2:21	58	16/5/2017 3:26	54	17/5/2017 4:31	57	18/5/2017 5:36	58	19/5/2017 6:41	47	20/5/2017 23:46	55
15/5/2017 2:26	58	16/5/2017 3:31	55	17/5/2017 4:36	56	18/5/2017 5:41	57	19/5/2017 6:46	60	20/5/2017 23:51	53
15/5/2017 2:31	58	16/5/2017 3:36	55	17/5/2017 4:41	56	18/5/2017 5:46	58	19/5/2017 6:51	60	20/5/2017 23:56	56
15/5/2017 2:36	58	16/5/2017 3:41	55	17/5/2017 4:46	56	18/5/2017 5:51	58	19/5/2017 6:56	60	21/5/2017 0:01	55
15/5/2017 2:41	58	16/5/2017 3:46	55	17/5/2017 4:51	57	18/5/2017 5:56	59	19/5/2017 23:01	60	21/5/2017 0:06	55
15/5/2017 2:46	58	16/5/2017 3:51	56	17/5/2017 4:56	57	18/5/2017 6:01	58	19/5/2017 23:06	60	21/5/2017 0:11	56
15/5/2017 2:51	57	16/5/2017 3:56	56	17/5/2017 5:01	56	18/5/2017 6:06	58	19/5/2017 23:11	60	21/5/2017 0:16	58
15/5/2017 2:56	58	16/5/2017 4:01	55	17/5/2017 5:06	57	18/5/2017 6:11	59	19/5/2017 23:16	60	21/5/2017 0:21	61
15/5/2017 3:01	58	16/5/2017 4:06	54	17/5/2017 5:11	5						


Real-time Noise Data		RTN4 (Causeway Bay Community Centre)							
21/5/2017 3:16	60	22/5/2017 4:21	57	23/5/2017 5:26	68	24/5/2017 6:31	70	25/5/2017 23:36	58
21/5/2017 3:21	61	22/5/2017 4:26	58	23/5/2017 5:31	68	24/5/2017 6:36	68	25/5/2017 23:41	58
21/5/2017 3:26	60	22/5/2017 4:31	59	23/5/2017 5:36	68	24/5/2017 6:41	62	25/5/2017 23:46	58
21/5/2017 3:31	61	22/5/2017 4:36	59	23/5/2017 5:41	68	24/5/2017 6:46	59	25/5/2017 23:51	58
21/5/2017 3:36	61	22/5/2017 4:41	58	23/5/2017 5:46	68	24/5/2017 6:51	54	25/5/2017 23:56	60
21/5/2017 3:41	61	22/5/2017 4:46	58	23/5/2017 5:51	68	24/5/2017 6:56	72	26/5/2017 0:01	59
21/5/2017 3:46	61	22/5/2017 4:51	58	23/5/2017 5:56	68	24/5/2017 23:01	59	26/5/2017 0:06	58
21/5/2017 3:51	61	22/5/2017 4:56	58	23/5/2017 6:01	68	24/5/2017 23:06	59	26/5/2017 0:11	58
21/5/2017 3:56	61	22/5/2017 5:01	58	23/5/2017 6:06	68	24/5/2017 23:11	59	26/5/2017 0:16	58
21/5/2017 4:01	61	22/5/2017 5:06	58	23/5/2017 6:11	68	24/5/2017 23:16	59	26/5/2017 0:21	58
21/5/2017 4:06	61	22/5/2017 5:11	57	23/5/2017 6:16	68	24/5/2017 23:21	60	26/5/2017 0:26	58
21/5/2017 4:11	61	22/5/2017 5:16	57	23/5/2017 6:21	68	24/5/2017 23:26	59	26/5/2017 0:31	58
21/5/2017 4:16	61	22/5/2017 5:21	57	23/5/2017 6:26	68	24/5/2017 23:31	60	26/5/2017 0:36	58
21/5/2017 4:21	61	22/5/2017 5:26	58	23/5/2017 6:31	68	24/5/2017 23:36	59	26/5/2017 0:41	58
21/5/2017 4:26	61	22/5/2017 5:31	58	23/5/2017 6:36	68	24/5/2017 23:41	59	26/5/2017 0:46	57
21/5/2017 4:31	61	22/5/2017 5:36	59	23/5/2017 6:41	68	24/5/2017 23:46	59	26/5/2017 0:51	57
21/5/2017 4:36	61	22/5/2017 5:41	59	23/5/2017 6:46	68	24/5/2017 23:51	58	26/5/2017 0:56	57
21/5/2017 4:41	61	22/5/2017 5:46	59	23/5/2017 6:51	68	24/5/2017 23:56	58	26/5/2017 1:01	58
21/5/2017 4:46	61	22/5/2017 5:51	59	23/5/2017 6:56	68	25/5/2017 0:01	59	26/5/2017 1:06	58
21/5/2017 4:51	61	22/5/2017 5:56	58	23/5/2017 23:01	60	25/5/2017 0:06	58	26/5/2017 1:11	58
21/5/2017 4:56	61	22/5/2017 6:01	59	23/5/2017 23:06	59	25/5/2017 0:11	59	26/5/2017 1:16	57
21/5/2017 5:01	61	22/5/2017 6:06	59	23/5/2017 23:11	59	25/5/2017 0:16	58	26/5/2017 1:21	57
21/5/2017 5:06	61	22/5/2017 6:11	60	23/5/2017 23:16	59	25/5/2017 0:21	58	26/5/2017 1:26	58
21/5/2017 5:11	61	22/5/2017 6:16	60	23/5/2017 23:21	59	25/5/2017 0:26	57	26/5/2017 1:31	57
21/5/2017 5:16	62	22/5/2017 6:21	60	23/5/2017 23:26	59	25/5/2017 0:31	58	26/5/2017 1:36	57
21/5/2017 5:21	62	22/5/2017 6:26	60	23/5/2017 23:31	59	25/5/2017 0:36	57	26/5/2017 1:41	57
21/5/2017 5:26	62	22/5/2017 6:31	61	23/5/2017 23:36	59	25/5/2017 0:41	57	26/5/2017 1:46	56
21/5/2017 5:31	63	22/5/2017 6:36	62	23/5/2017 23:41	58	25/5/2017 0:46	58	26/5/2017 1:51	56
21/5/2017 5:36	63	22/5/2017 6:41	62	23/5/2017 23:46	58	25/5/2017 0:51	58	26/5/2017 1:56	56
21/5/2017 5:41	63	22/5/2017 6:46	62	23/5/2017 23:51	58	25/5/2017 0:56	57	26/5/2017 2:01	56
21/5/2017 5:46	63	22/5/2017 6:51	61	23/5/2017 23:56	57	25/5/2017 1:01	57	26/5/2017 2:06	56
21/5/2017 5:51	64	22/5/2017 6:56	60	24/5/2017 0:01	58	25/5/2017 1:06	57	26/5/2017 2:11	55
21/5/2017 5:56	66	22/5/2017 23:01	56	24/5/2017 0:06	58	25/5/2017 1:11	57	26/5/2017 2:16	55
21/5/2017 6:01	63	22/5/2017 23:06	57	24/5/2017 0:11	58	25/5/2017 1:16	57	26/5/2017 2:21	56
21/5/2017 6:06	63	22/5/2017 23:11	57	24/5/2017 0:16	58	25/5/2017 1:21	56	26/5/2017 2:26	56
21/5/2017 6:11	63	22/5/2017 23:16	54	24/5/2017 0:21	58	25/5/2017 1:26	57	26/5/2017 2:31	55
21/5/2017 6:16	63	22/5/2017 23:21	49	24/5/2017 0:26	58	25/5/2017 1:31	56	26/5/2017 2:36	56
21/5/2017 6:21	63	22/5/2017 23:26	46	24/5/2017 0:31	58	25/5/2017 1:36	56	26/5/2017 2:41	55
21/5/2017 6:26	63	22/5/2017 23:31	52	24/5/2017 0:36	59	25/5/2017 1:41	56	26/5/2017 2:46	55
21/5/2017 6:31	63	22/5/2017 23:36	51	24/5/2017 0:41	57	25/5/2017 1:46	56	26/5/2017 2:51	55
21/5/2017 6:36	62	22/5/2017 23:41	51	24/5/2017 0:46	57	25/5/2017 1:51	57	26/5/2017 2:56	56
21/5/2017 6:41	63	22/5/2017 23:46	38	24/5/2017 0:51	57	25/5/2017 1:56	56	26/5/2017 3:01	54
21/5/2017 6:46	63	22/5/2017 23:51	53	24/5/2017 0:56	56	25/5/2017 2:01	56	26/5/2017 3:06	55
21/5/2017 6:51	62	22/5/2017 23:56	55	24/5/2017 1:01	58	25/5/2017 2:06	57	26/5/2017 3:11	55
21/5/2017 6:56	62	23/5/2017 0:01	52	24/5/2017 1:06	57	25/5/2017 2:11	55	26/5/2017 3:16	55
21/5/2017 23:01	60	23/5/2017 0:06	41	24/5/2017 1:11	58	25/5/2017 2:16	55	26/5/2017 3:21	54
21/5/2017 23:06	60	23/5/2017 0:11	44	24/5/2017 1:16	55	25/5/2017 2:21	56	26/5/2017 3:26	55
21/5/2017 23:11	61	23/5/2017 0:16	55	24/5/2017 1:21	56	25/5/2017 2:26	56	26/5/2017 3:31	56
21/5/2017 23:16	60	23/5/2017 0:21	52	24/5/2017 1:26	57	25/5/2017 2:31	56	26/5/2017 3:36	55
21/5/2017 23:21	59	23/5/2017 0:26	50	24/5/2017 1:31	56	25/5/2017 2:36	55	26/5/2017 3:41	54
21/5/2017 23:26	60	23/5/2017 0:31	51	24/5/2017 1:36	57	25/5/2017 2:41	56	26/5/2017 3:46	55
21/5/2017 23:31	60	23/5/2017 0:36	49	24/5/2017 1:41	56	25/5/2017 2:46	56	26/5/2017 3:51	55
21/5/2017 23:36	60	23/5/2017 0:41	47	24/5/2017 1:46	56	25/5/2017 2:51	54	26/5/2017 3:56	54
21/5/2017 23:41	60	23/5/2017 0:46	60	24/5/2017 1:51	55	25/5/2017 2:56	55	26/5/2017 4:01	55
21/5/2017 23:46	60	23/5/2017 0:51	61	24/5/2017 1:56	55	25/5/2017 3:01	55	26/5/2017 4:06	55
21/5/2017 23:51	60	23/5/2017 0:56	39	24/5/2017 2:01	55	25/5/2017 3:06	55	26/5/2017 4:11	55
21/5/2017 23:56	62	23/5/2017 1:01	61	24/5/2017 2:06	55	25/5/2017 3:11	55	26/5/2017 4:16	54
22/5/2017 0:01	62	23/5/2017 1:06	61	24/5/2017 2:11	54	25/5/2017 3:16	54	26/5/2017 4:21	55
22/5/2017 0:06	62	23/5/2017 1:11	60	24/5/2017 2:16	55	25/5/2017 3:21	55	26/5/2017 4:26	55
22/5/2017 0:11	62	23/5/2017 1:16	60	24/5/2017 2:21	55	25/5/2017 3:26	55	26/5/2017 4:31	54
22/5/2017 0:16	62	23/5/2017 1:21	60	24/5/2017 2:26	54	25/5/2017 3:31	56	26/5/2017 4:36	54
22/5/2017 0:21	61	23/5/2017 1:26	60	24/5/2017 2:31	55	25/5/2017 3:36	56	26/5/2017 4:41	55
22/5/2017 0:26	61	23/5/2017 1:31	60	24/5/2017 2:36	55	25/5/2017 3:41	55	26/5/2017 4:46	56
22/5/2017 0:31	61	23/5/2017 1:36	61	24/5/2017 2:41	55	25/5/2017 3:46	55	26/5/2017 4:51	56
22/5/2017 0:36	61	23/5/2017 1:41	61	24/5/2017 2:46	54	25/5/2017 3:51	55	26/5/2017 4:56	56
22/5/2017 0:41	61	23/5/2017 1:46	60	24/5/2017 2:51	55	25/5/2017 3:56	54	26/5/2017 5:01	55
22/5/2017 0:46	61	23/5/2017 1:51	59	24/5/2017 2:56	56	25/5/2017 4:01	55	26/5/2017 5:06	56
22/5/2017 0:51	61	23/5/2017 1:56	60	24/5/2017 3:01	55	25/5/2017 4:06	55	26/5/2017 5:11	55
22/5/2017 0:56	61	23/5/2017 2:01	60	24/5/2017 3:06	54	25/5/2017 4:11	54	26/5/2017 5:16	57
22/5/2017 1:01	61	23/5/2017 2:06	60	24/5/2017 3:11	54	25/5/2017 4:16	54	26/5/2017 5:21	56
22/5/2017 1:06	61	23/5/2017 2:11	60	24/5/2017 3:16	55	25/5/2017 4:21	55	26/5/2017 5:26	55
22/5/2017 1:11	61	23/5/2017 2:16	61	24/5/2017 3:21	54	25/5/2017 4:26	55	26/5/2017 5:31	57
22/5/2017 1:16	61	23/5/2017 2:21	61	24/5/2017 3:26	54	25/5/2017 4:31	54	26/5/2017 5:36	58
22/5/2017 1:21	61	23/5/2017 2:26	61	24/5/2017 3:31	55	25/5/2017 4:36	55	26/5/2017 5:41	58
22/5/2017 1:26	61	23/5/2017 2:31	60	24/5/2017 3:36	55	25/5/2017 4:41	55	26/5/2017 5:46	57
22/5/2017 1:31	61	23/5/2017 2:36	42	24/5/2017 3:41	55	25/5/2017 4:46	55	26/5/2017 5:51	58
22/5/2017 1:36	61	23/5/2017 2:41	61	24/5/2017 3:46	54	25/5/2017 4:51	56	26/5/2017 5:56	58
22/5/2017 1:41	60	23/5/2017 2:46	61	24/5/2017 3:51	54	25/5/2017 4:56	56	26/5/2017 6:01	58
22/5/2017 1:46	60	23/5/2017 2:51	60	24/5/2017 3:56	54	25/5/2017 5:01	55	26/5/2017 6:06	58
22/5/2017 1:51	60	23/5/2017 2:56	60	24/5/2017 4:01	54	25/5/2017 5:06	56	26/5/2017 6:11	58
22/5/2017 1:56	60	23/5/2017 3:01	60	24/5/2017 4:06	54	25/5/2017 5:11	56	26/5/2017 6:16	59
22/5/2017 2:01	60	23/5/2017 3:06	60	24/5/2017 4:11	54	25/5/2017 5:16	56	26/5/2017 6:21	59
22/5/2017 2:06	60	23/5/2017 3:11	60	24/5/2017 4:16	54	25/5/2017 5:21	57	26/5/2017 6:26	59
22/5/2017 2:11	59	23/5/2017 3:16	61	24/5/2017 4:21	55	25/5/2017 5:26	56	26/5/2017 6:31	59
22/5/2017 2:16	60	23/5/2017 3:21	60	24/5/2017 4:26	55	25/5/2017 5:31	59	26/5/2017 6:36	60
22/5/2017 2:21	60	23/5/2017 3:26	64	24/5/2017 4:31	56	25/5/2017 5:36	57	26/5/2017 6:41	61
22/5/2017 2:26	60	23/5/2017 3:31	68	24/5/2017 4:36	55	25/5/2017 5:41	57	26/5/2017 6:46	61
22/5/2017 2:31	60	23/5/2017 3:36	68	24/5/2017 4:41	54	25/5/2017 5:46	58	26/5/2017 6:51	61
22/5/2017 2:36	60	23/5/2017 3:41	68	24/5/2017 4:46	54	25/5/2017 5:51	58	26/5/2017 6:56	60
22/5/2017 2:41	61	23/5/2017 3:46	68	24/5/2017 4:51	55	25/5/2017 5:56	58	26/5/2017 23:01	60
22/5/2017 2:46	60	23/5/2017 3:51	68	24/5/20					

Graphic Presentation of Real Time Noise Monitoring Result (RTN1-Food and Environmental Hygiene Department Depot)

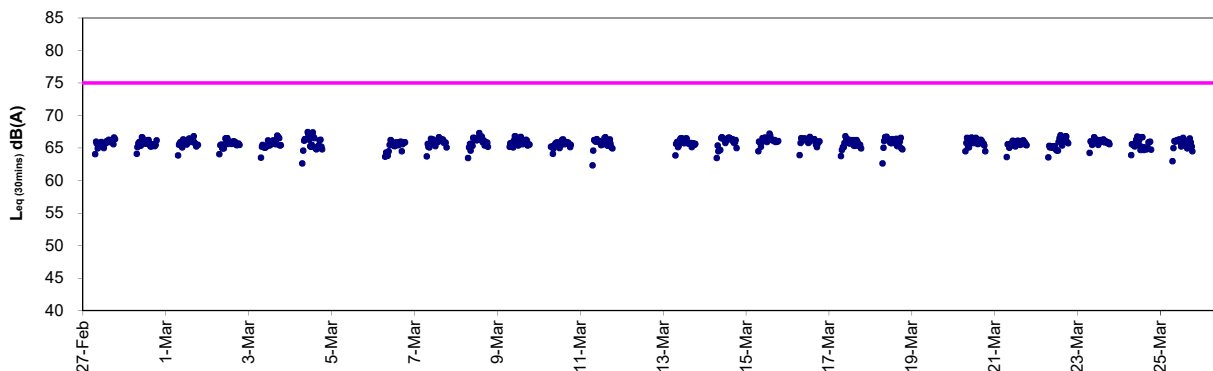
Day Time (0700 -1900 hrs on normal weekdays)



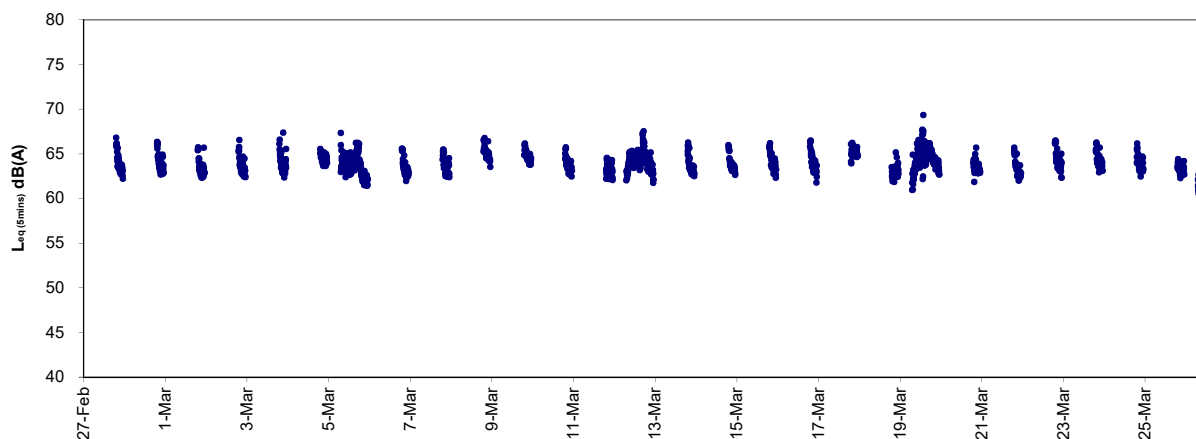
Restricted hours (1900 - 2300) on normal weekdays and 0700 - 2300 hrs on public holidays)



Night Time (2300 - 0700hrs)

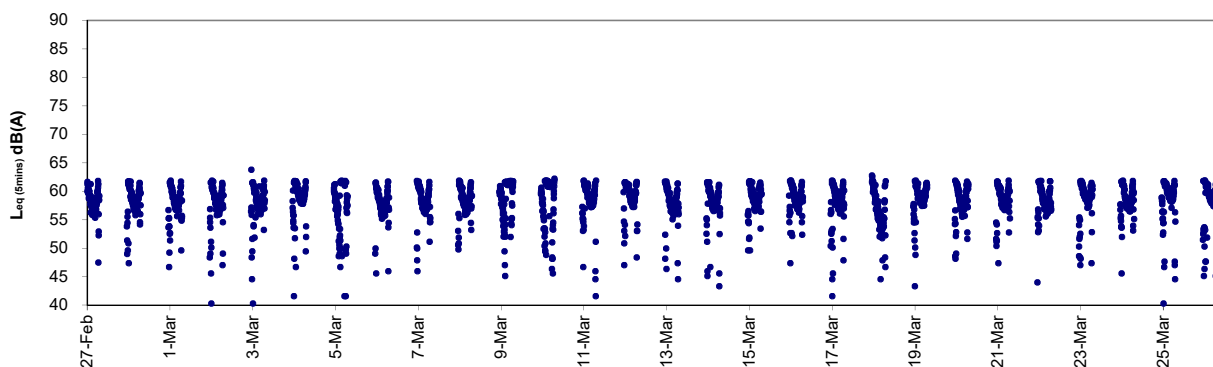

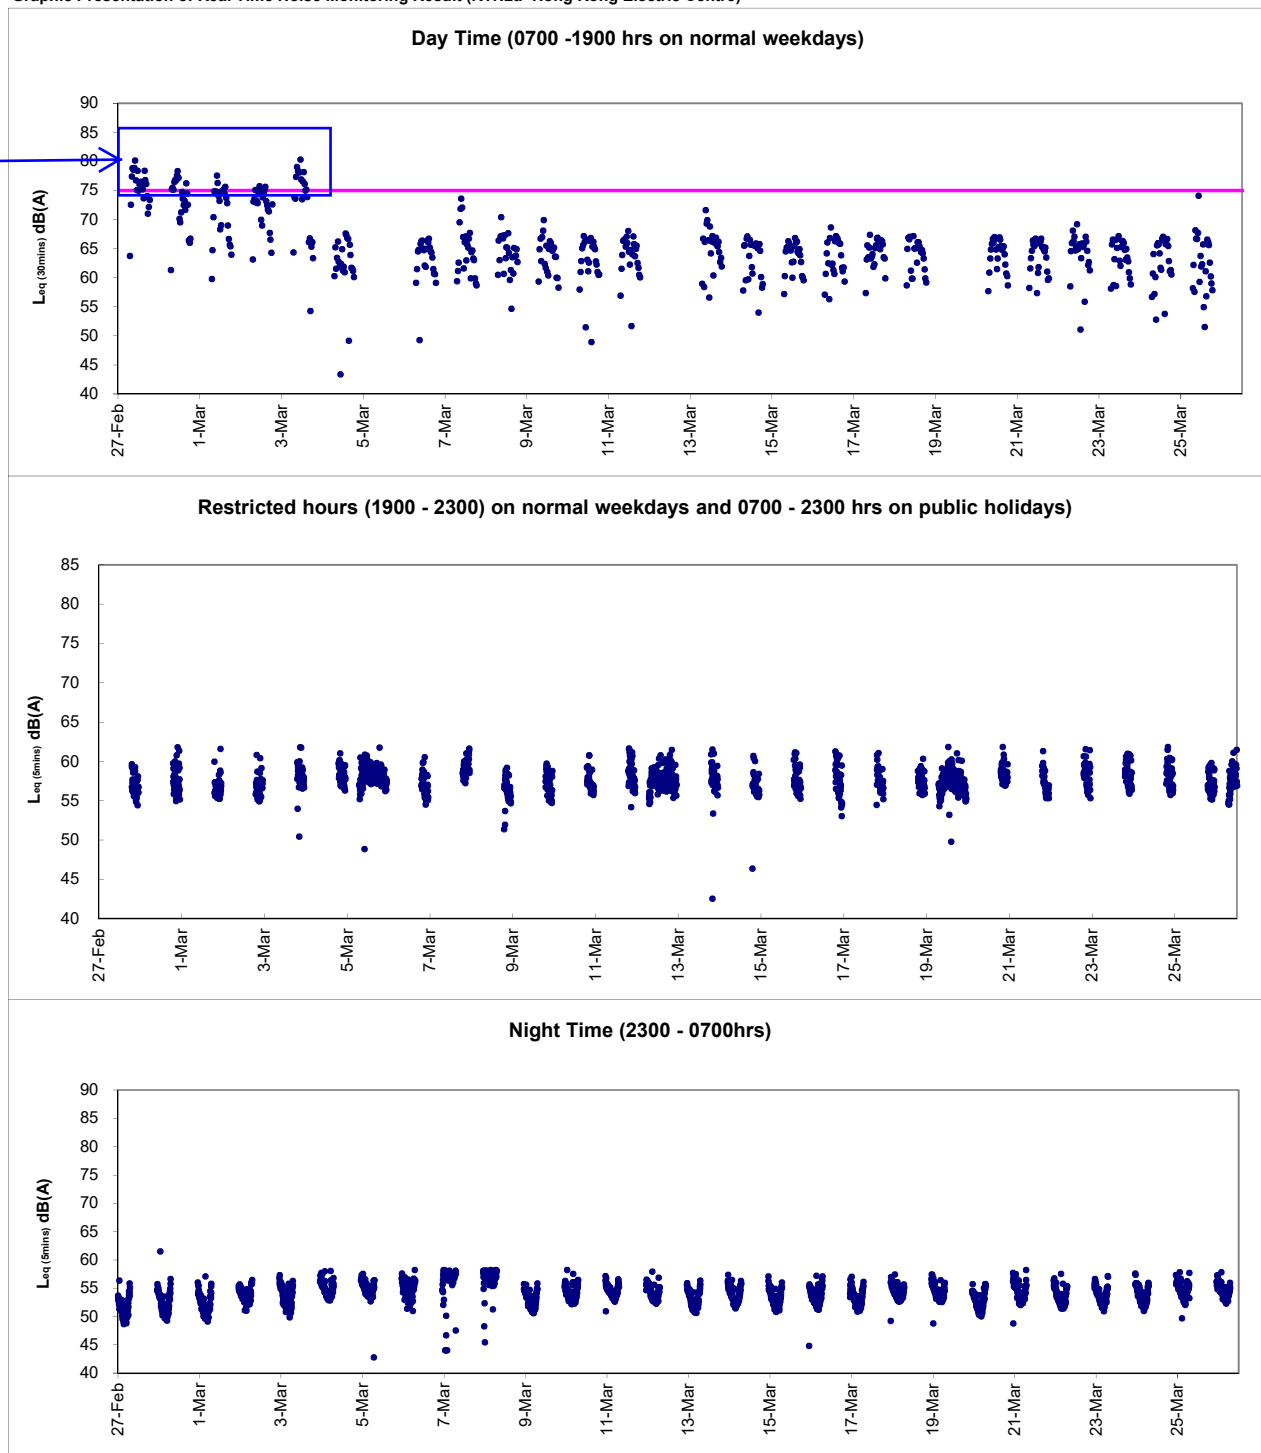
Graphic Presentation of Real Time Noise Monitoring Result (RTN2a- Hong Kong Electric Centre)




After checking with Contractor of HY/2009/19, sheet piling, pre bored drilling and breaking works were conducted on 27, 28 February and 01, 02 and 03 March 2017 and temporary noise barrier was generally implemented and breaking works was conducted behind physical building structure while formworks, bar fixing and concreting works were conducted on 27, 28 February and 01, 02 and 03 March 2017 under Contract HY/2011/08 and no particular noise was considered for the works. Nevertheless, building construction works with breaking and hammering works under non-CWB private development site at Oil Street was conducted at the building level adjacent to the noise monitoring station and were considered as the major noise contribution across the monitoring period. As such, the exceedances were considered as non-Project related.

Graphic Presentation of Real Time Noise Monitoring Result (RTN3-Yu Lee Mo Fan Memorial School)

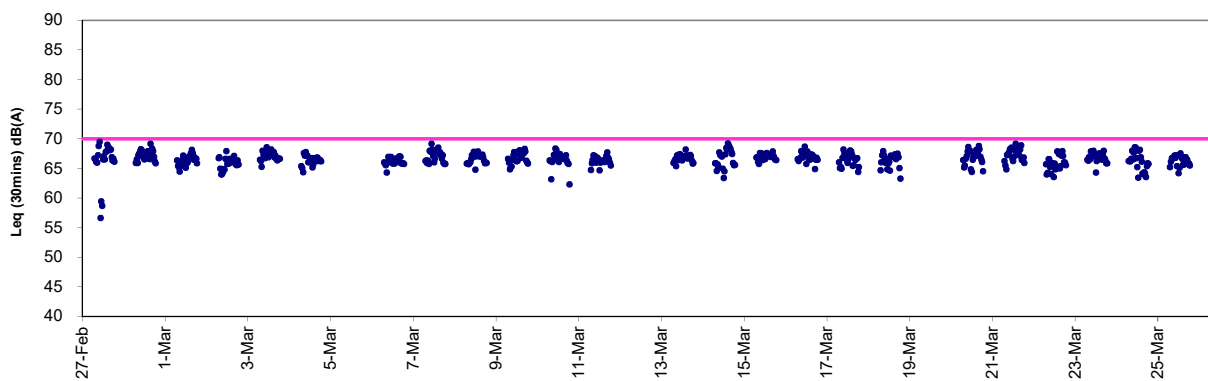
Day Time (0700 -1900 hrs on normal weekdays)



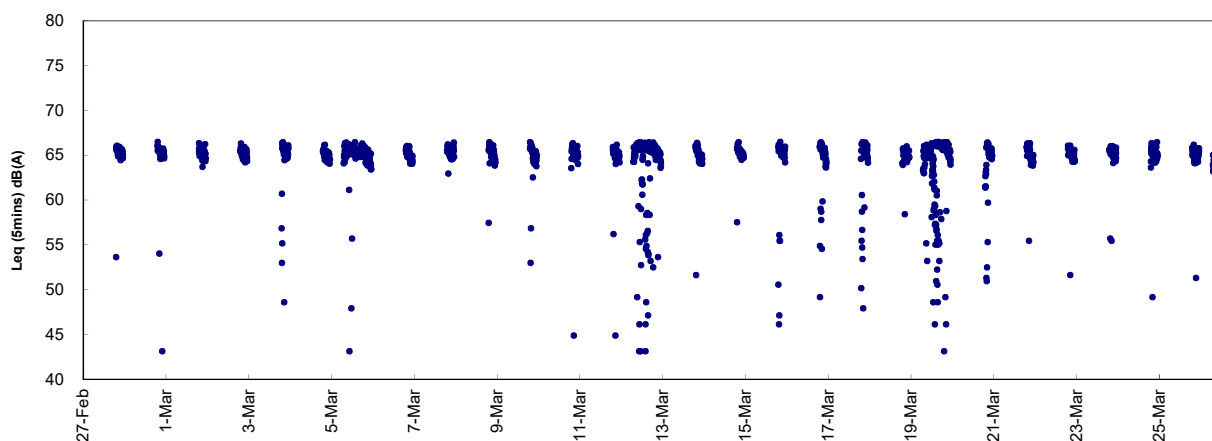Restricted hours (1900 - 2300) on normal weekdays and 0700 - 2300 hrs on public holidays)




Night Time (2300 - 0700hrs)

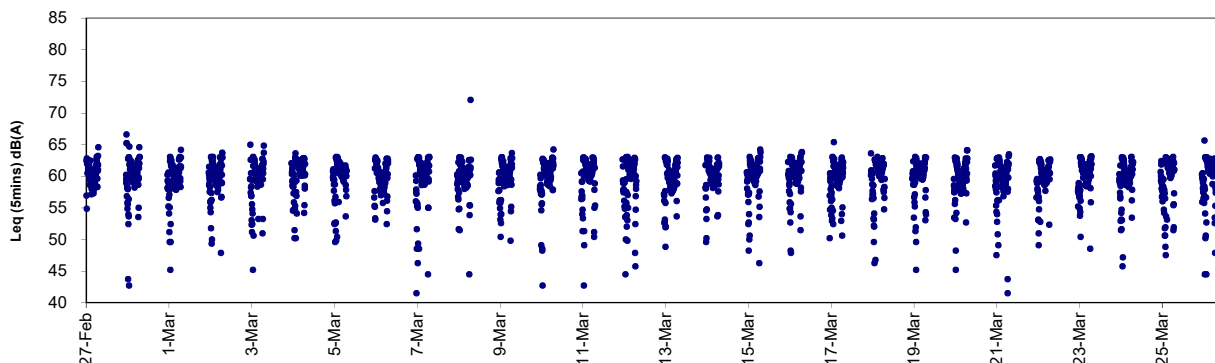




Graphic Presentation of Real Time Noise Monitoring Result (RTN4-Causeway Bay Community Centre)

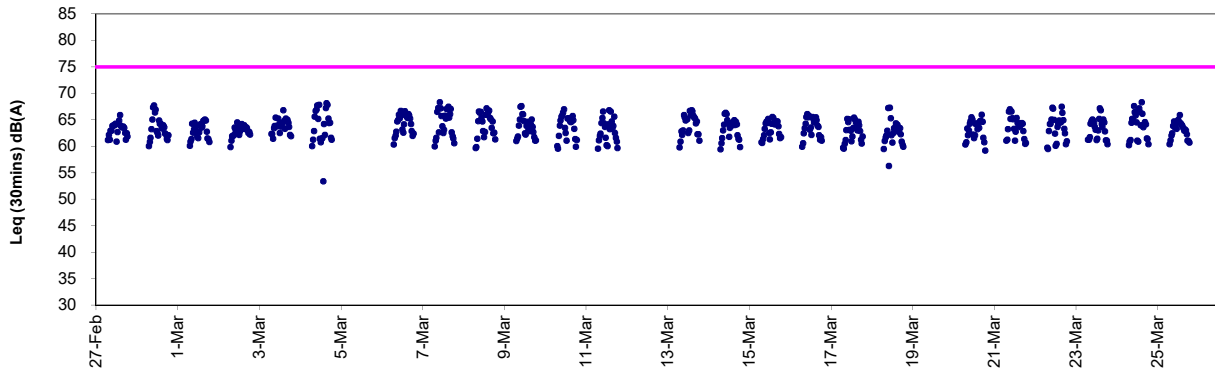
Day Time (0700 -1900 hrs on normal weekdays)



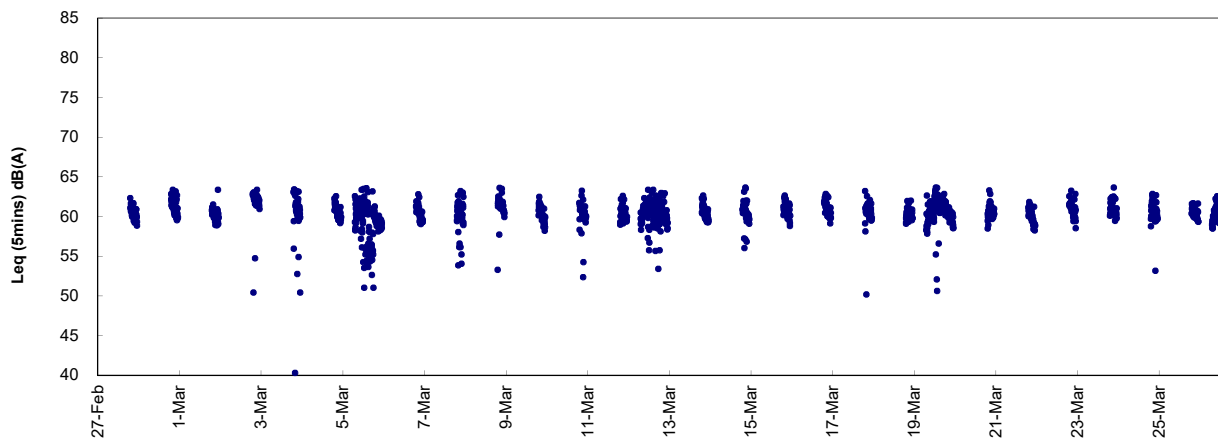Restricted hours (1900 - 2300) on normal weekdays and 0700 - 2300 hrs on public holidays)



Night Time (2300 - 0700hrs)

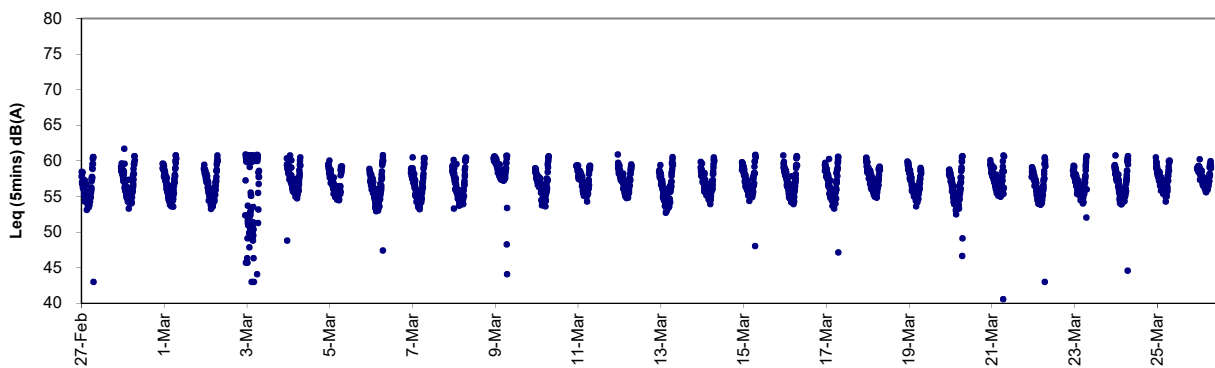




Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wan Chai Bypass


Sampling, Field Measurement and Testing Works (Stage 3)

Graphic Presentation of Real Time Noise Monitoring Result (RTN1-Food and Environmental Hygiene Department Depot)

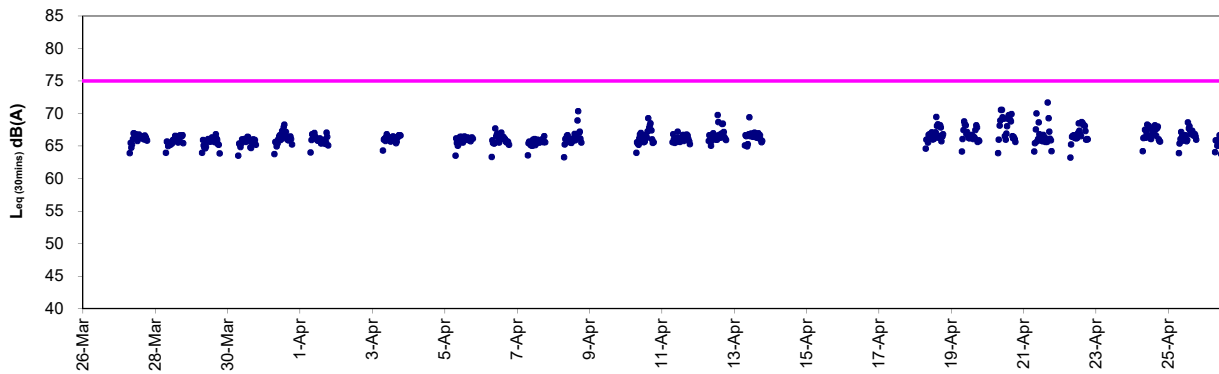
Day Time (0700 -1900 hrs on normal weekdays)



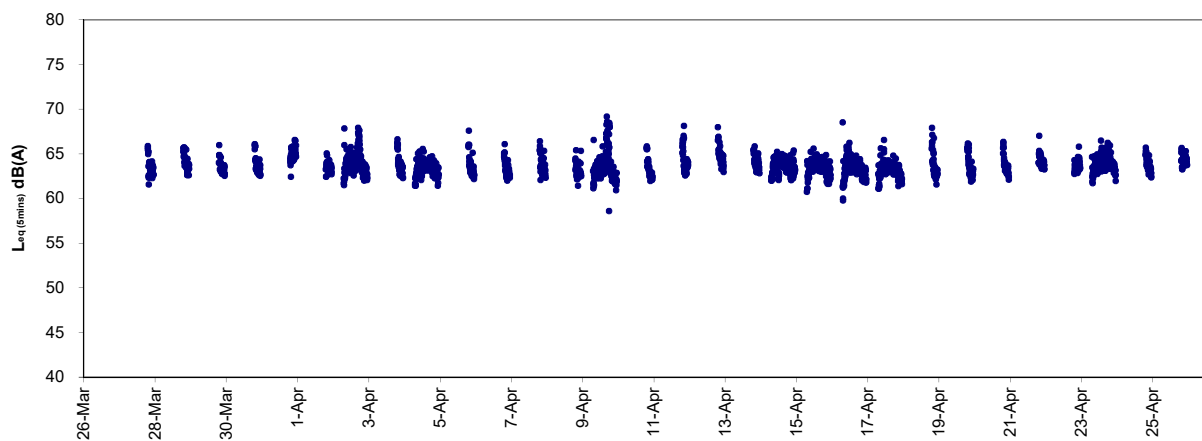Restricted hours (1900 - 2300) on normal weekdays and 0700 - 2300 hrs on public holidays)




Night Time (2300 - 0700hrs)

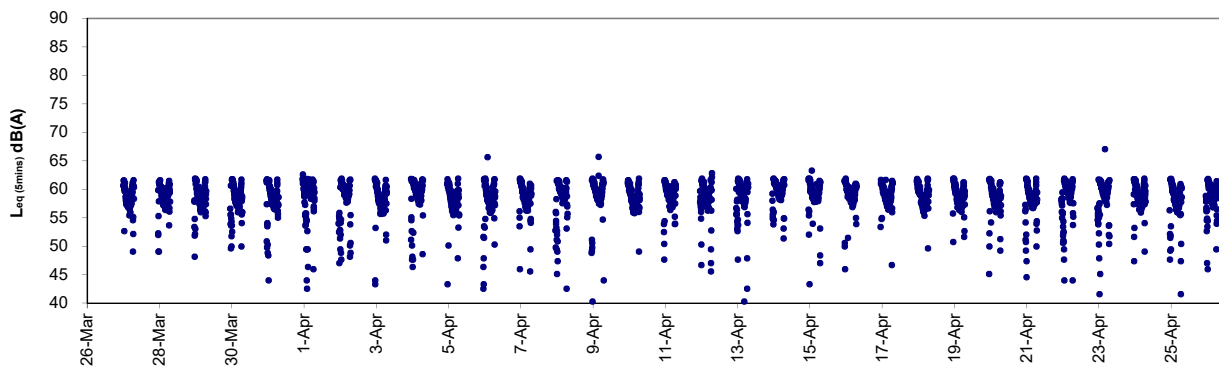




Graphic Presentation of Real Time Noise Monitoring Result (RTN2a- Hong Kong Electric Centre)

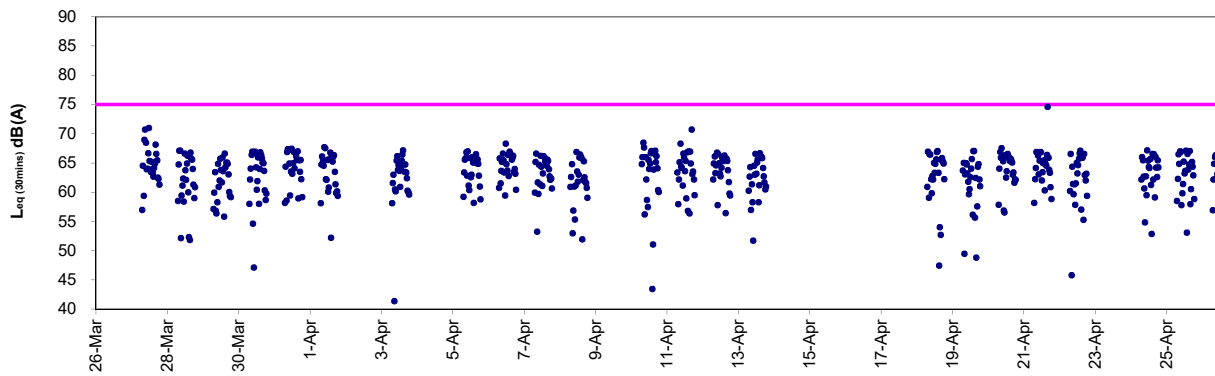
Day Time (0700 -1900 hrs on normal weekdays)



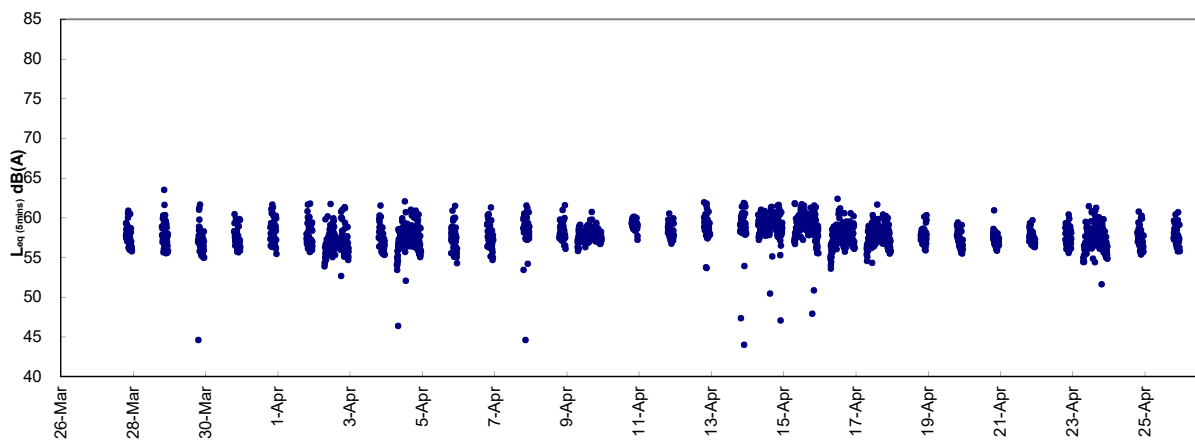Restricted hours (1900 - 2300) on normal weekdays and 0700 - 2300 hrs on public holidays)



Night Time (2300 - 0700hrs)

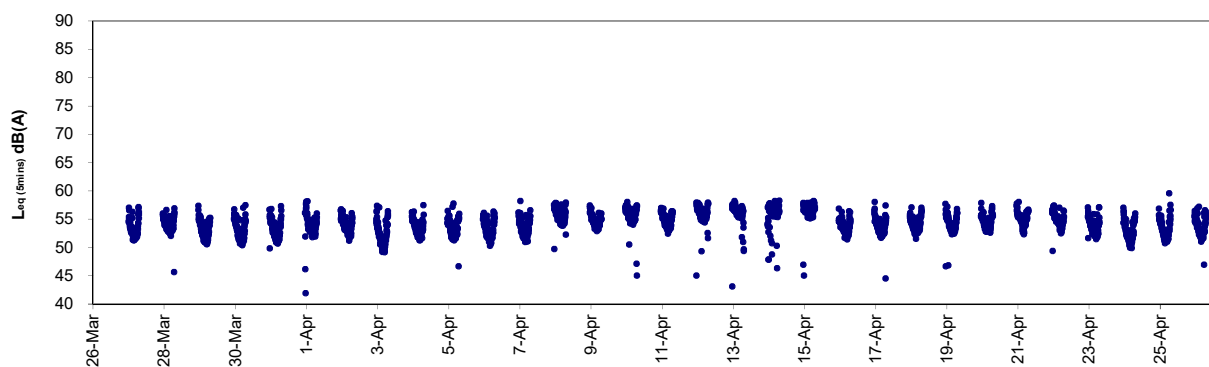




Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wan Chai Bypass


Sampling, Field Measurement and Testing Works (Stage 3)

Graphic Presentation of Real Time Noise Monitoring Result (RTN3-Yu Lee Mo Fan Memorial School)

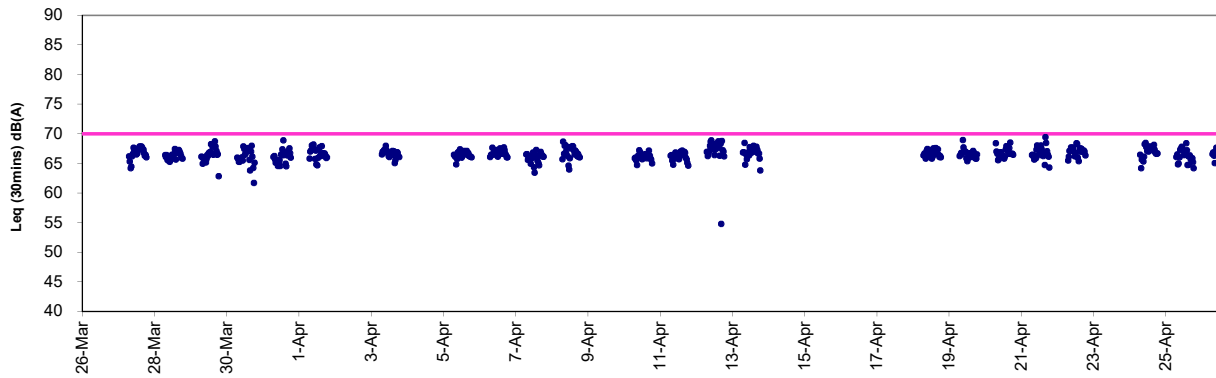
Day Time (0700 -1900 hrs on normal weekdays)



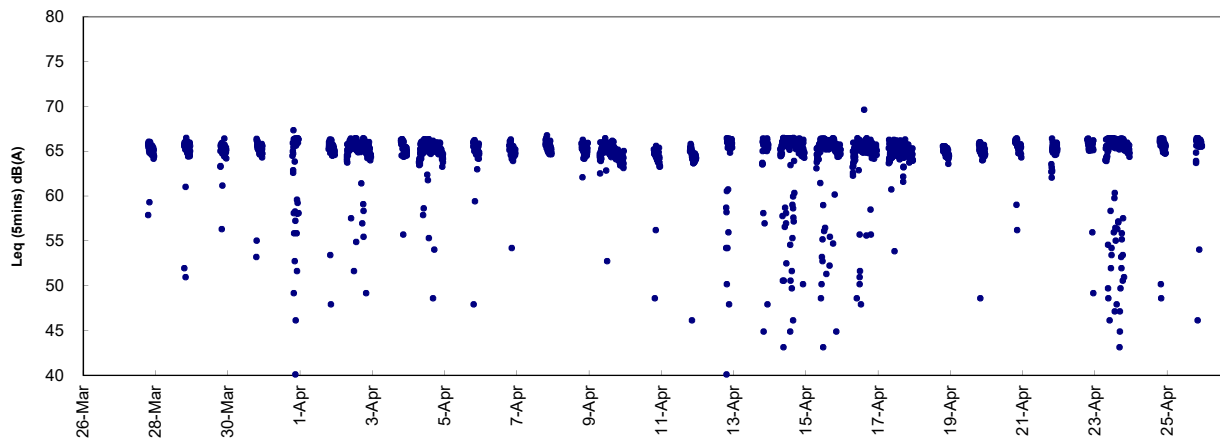
Restricted hours (1900 - 2300) on normal weekdays and 0700 - 2300 hrs on public holidays)



Night Time (2300 - 0700hrs)

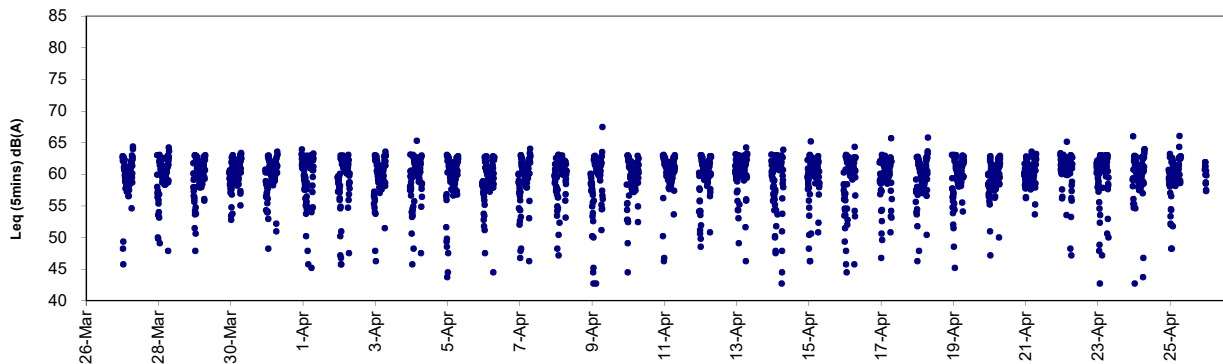

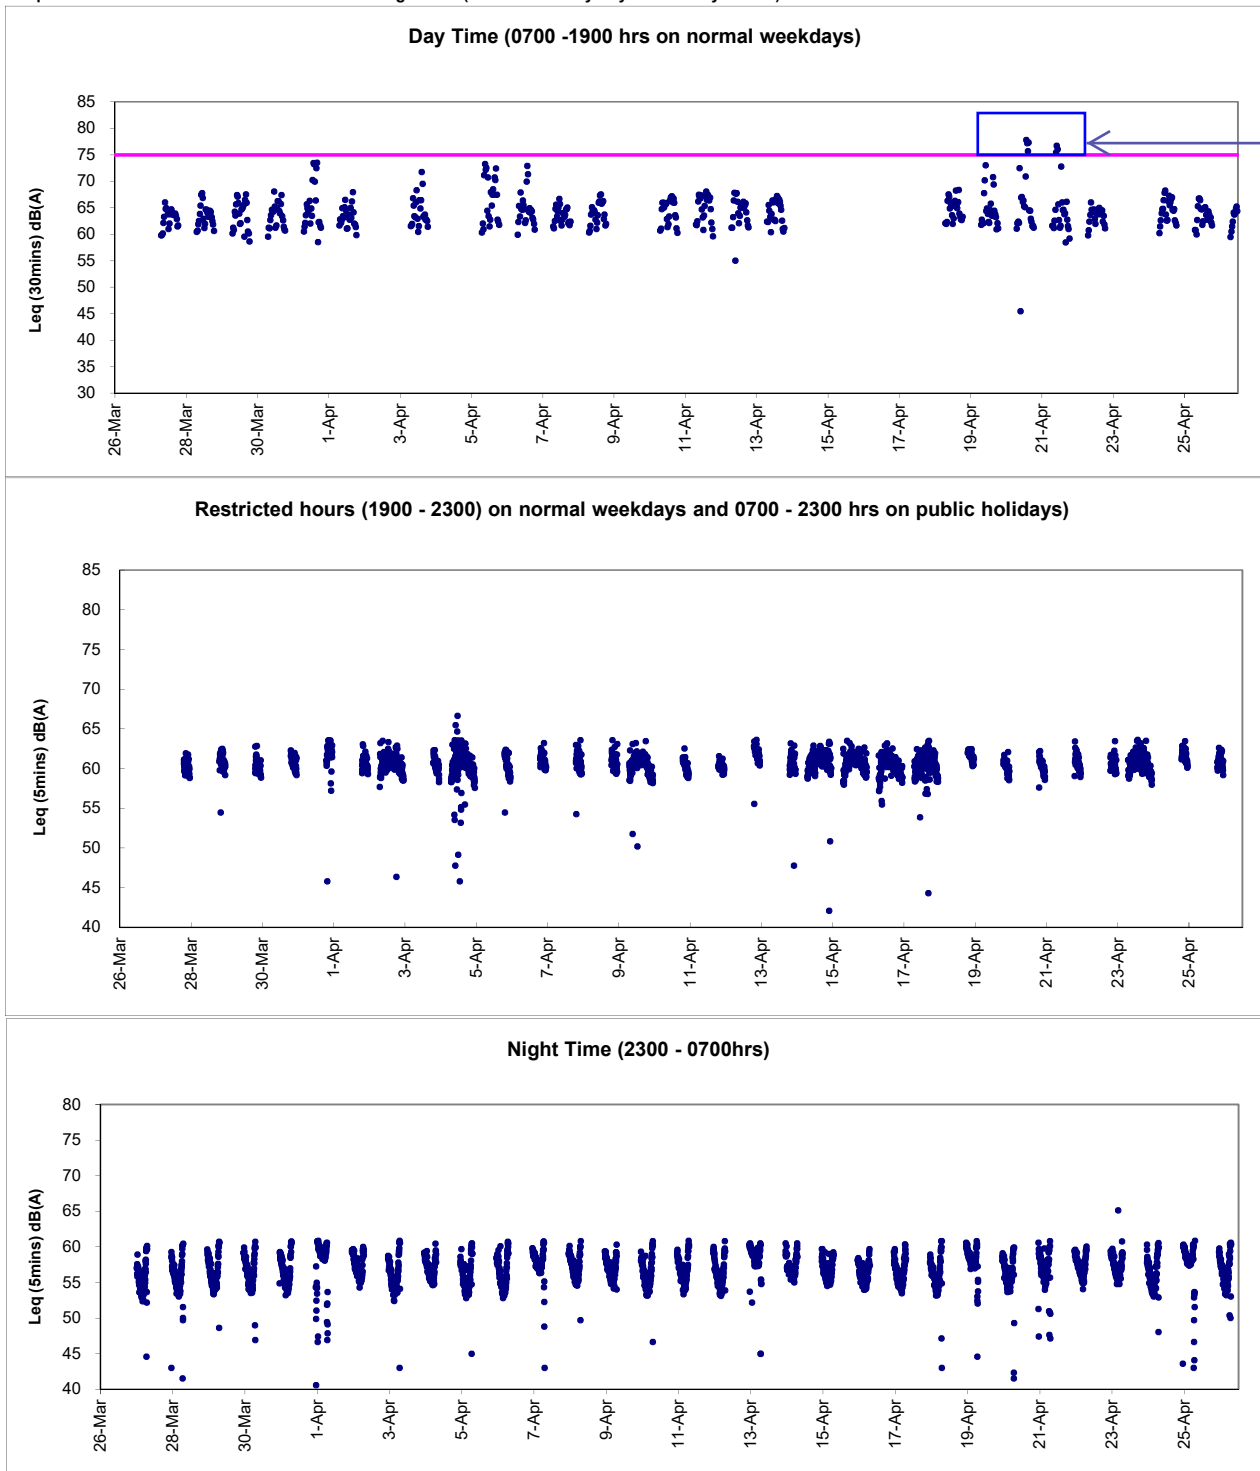Graphic Presentation of Real Time Noise Monitoring Result (RTN4-Causeway Bay Community Centre)



After checking with Contractors, no construction works activity was conducted under Contract HY/2009/19 and HY/2011/08 around the monitoring station on 20 and 21 April 2017 during the monitoring period while non - CWB breaking was observed conducted on the monitoring dates immediately next to the monitoring station. As such, the exceedances were concluded as non-Project related.



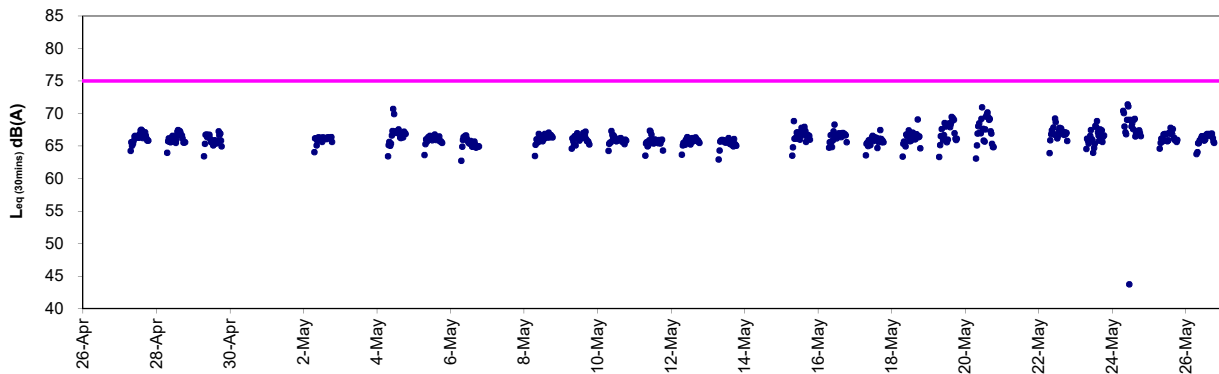
Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wan Chai Bypass


Sampling, Field Measurement and Testing Works (Stage 3)

Graphic Presentation of Real Time Noise Monitoring Result (RTN1-Food and Environmental Hygiene Department Depot)


Day Time (0700 -1900 hrs on normal weekdays)



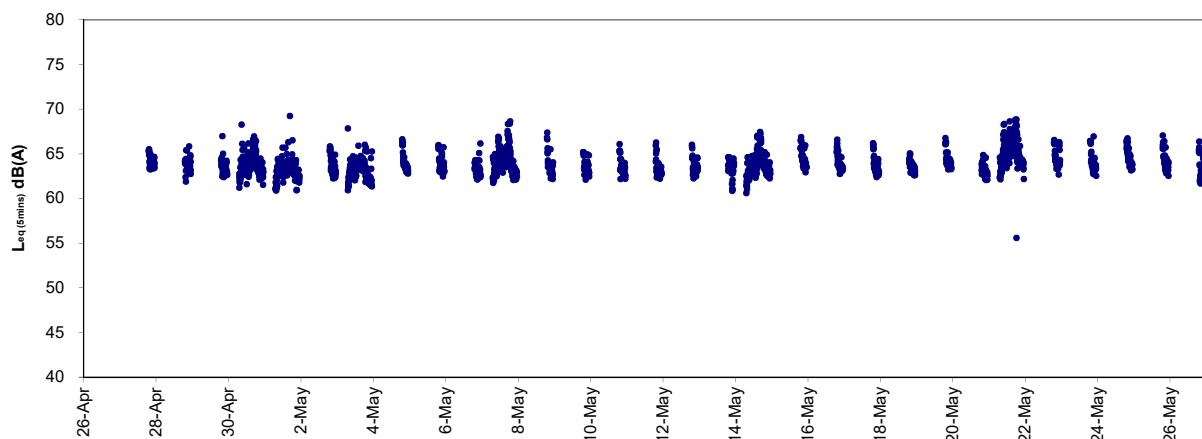
Restricted hours (1900 - 2300) on normal weekdays and 0700 - 2300 hrs on public holidays)



Night Time (2300 - 0700hrs)

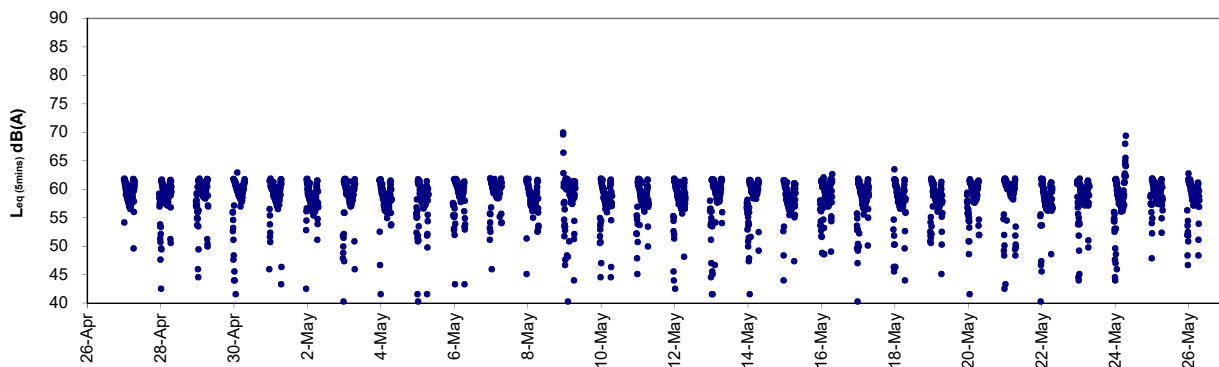


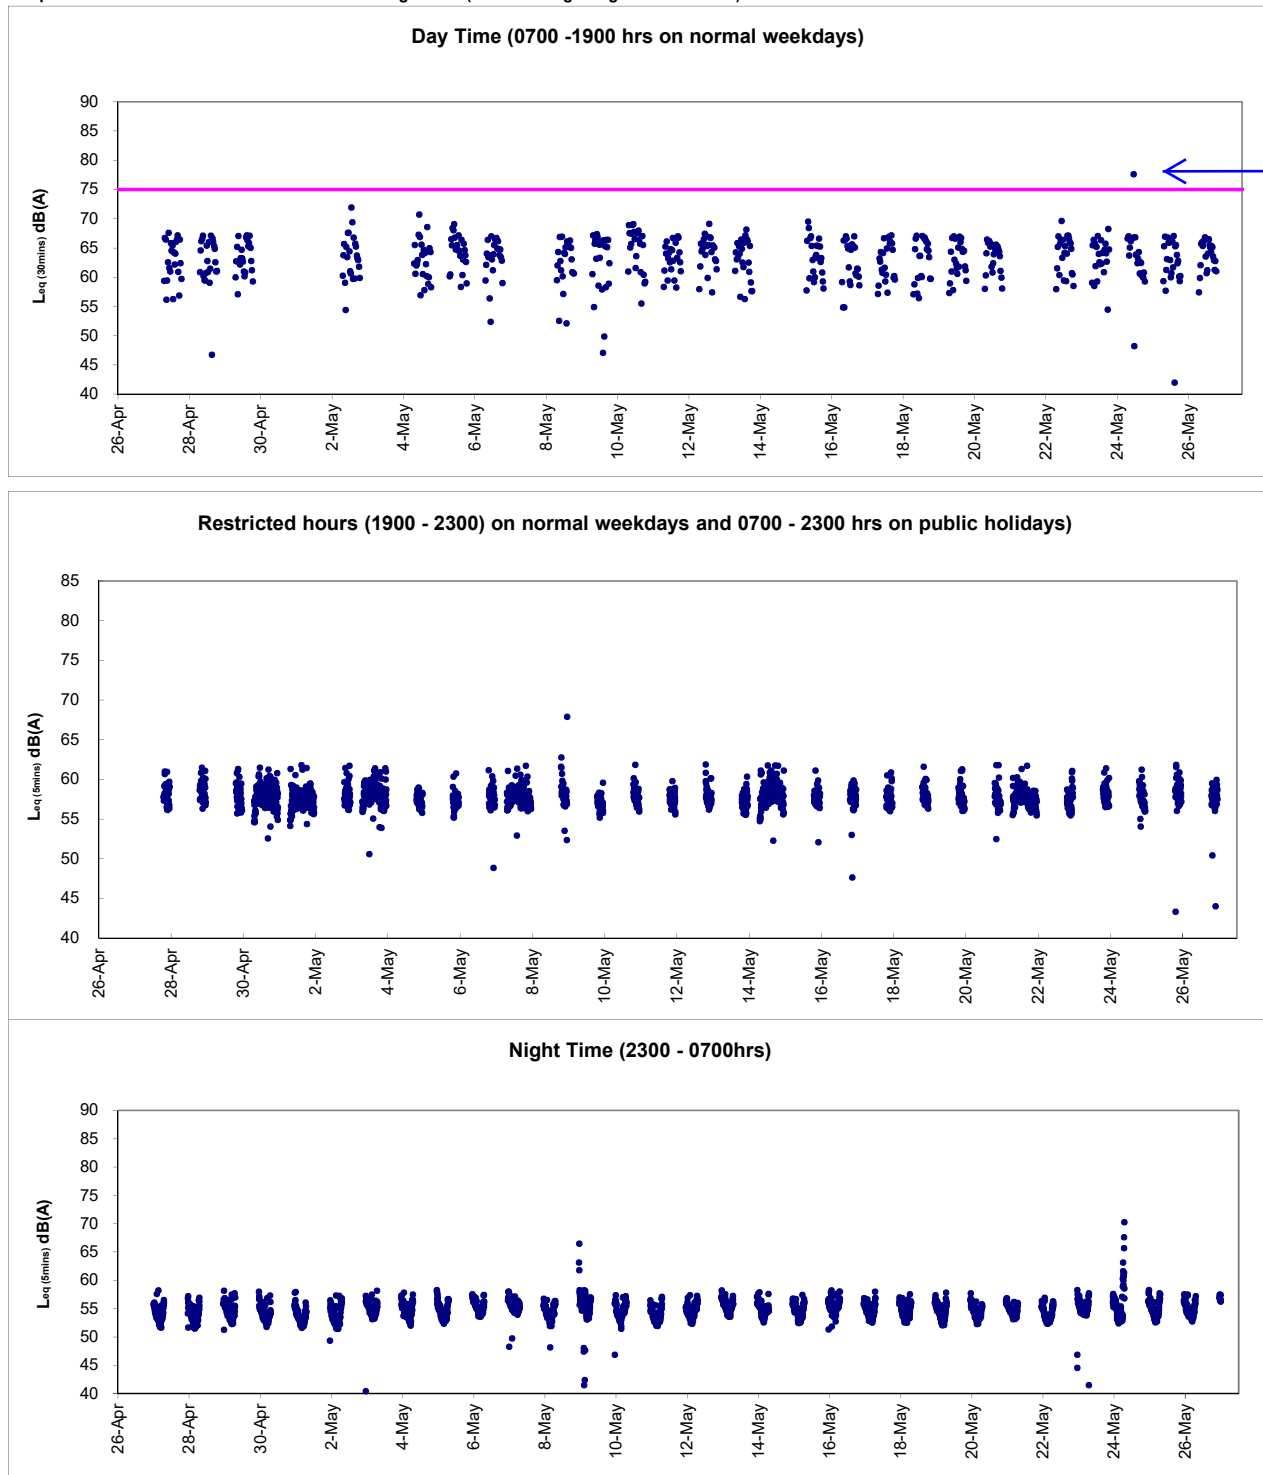Graphic Presentation of Real Time Noise Monitoring Result (RTN2a- Hong Kong Electric Centre)



After checking with Contractor of HY/2009/19, despite sheet piling works was conducted during the monitoring period and no construction works was conducted under HY/2011/08 during the monitoring period while adverse weather condition under Red Rainstorm Warning Signal was considered as the major noise contribution during monitoring. Hence, the exceedance was concluded as non-Project related.

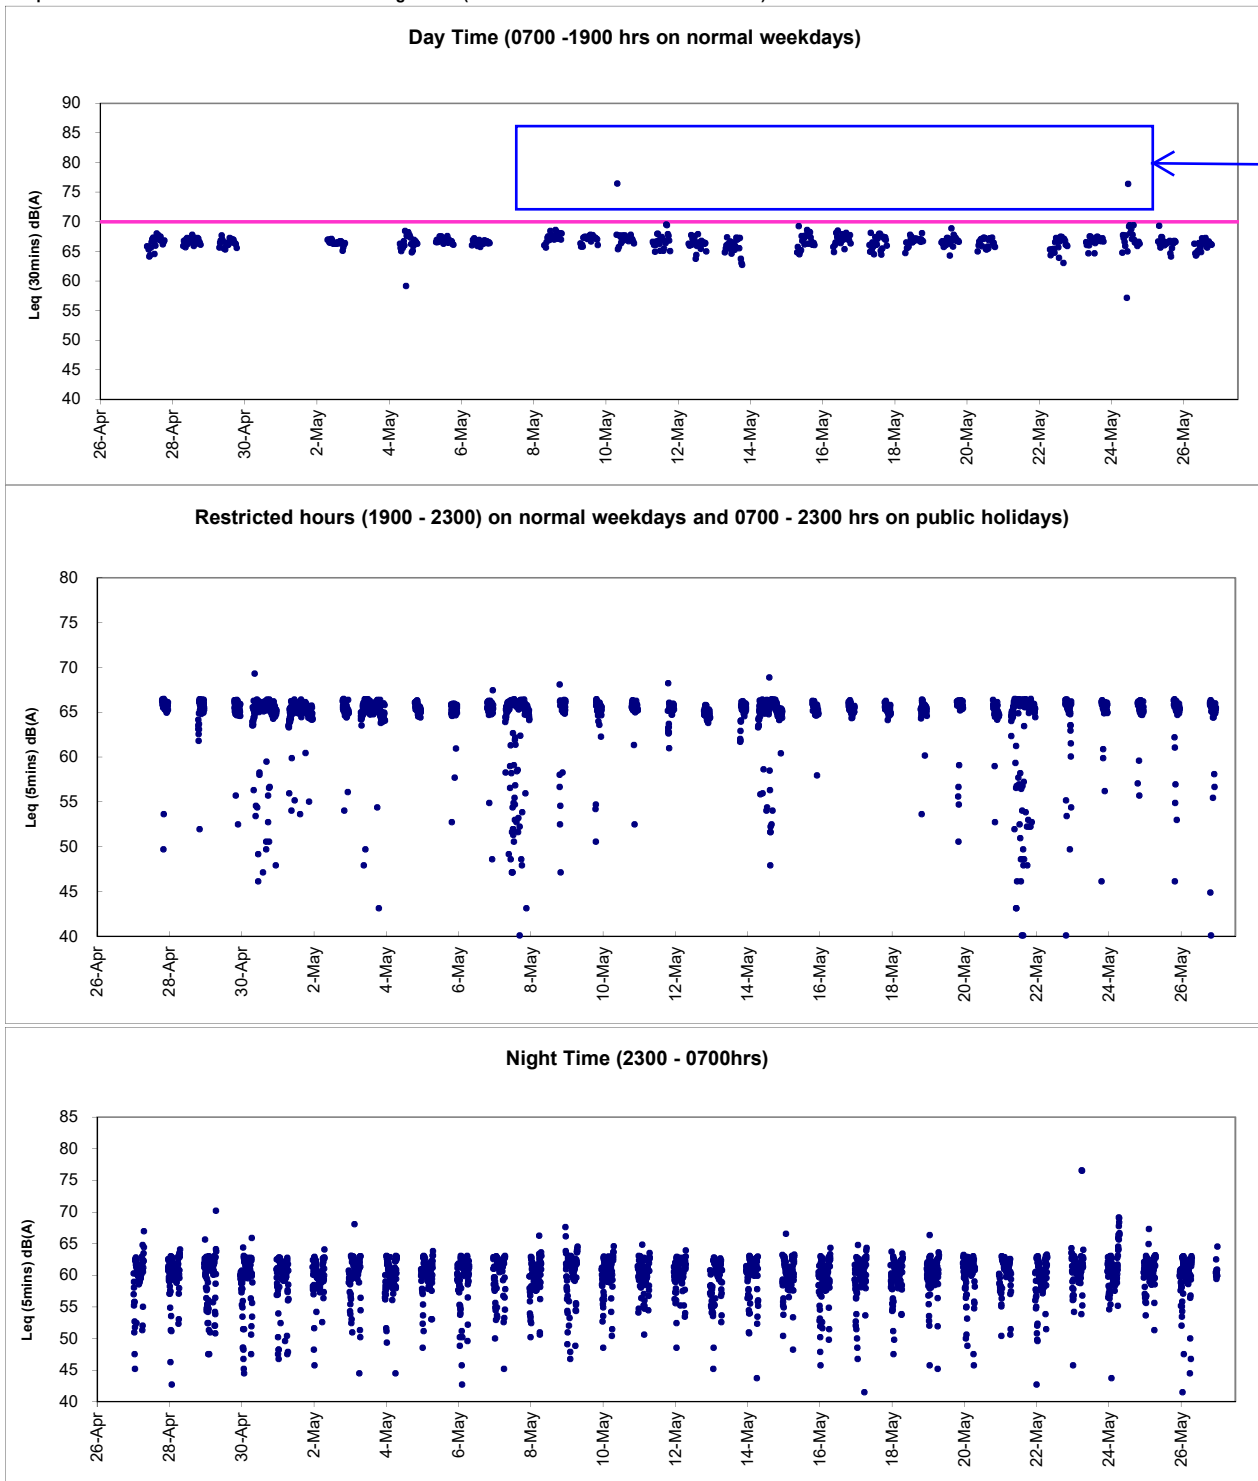Graphic Presentation of Real Time Noise Monitoring Result (RTN3-Yu Lee Mo Fan Memorial School)



After checking with Contractor of HY/2009/19, no construction works were conducted on 10 and 24 May 2017 around the monitoring location during the concerned period and hence the exceedances were considered to be non-Project related and potentially related to the traffic on 10 May 2017 and the adverse weather under Red Rainstorm Warning Signal on 24 May 2017.



Contract no. HK/2015/01

Wan Chai Development Phase II and Central-Wan Chai Bypass

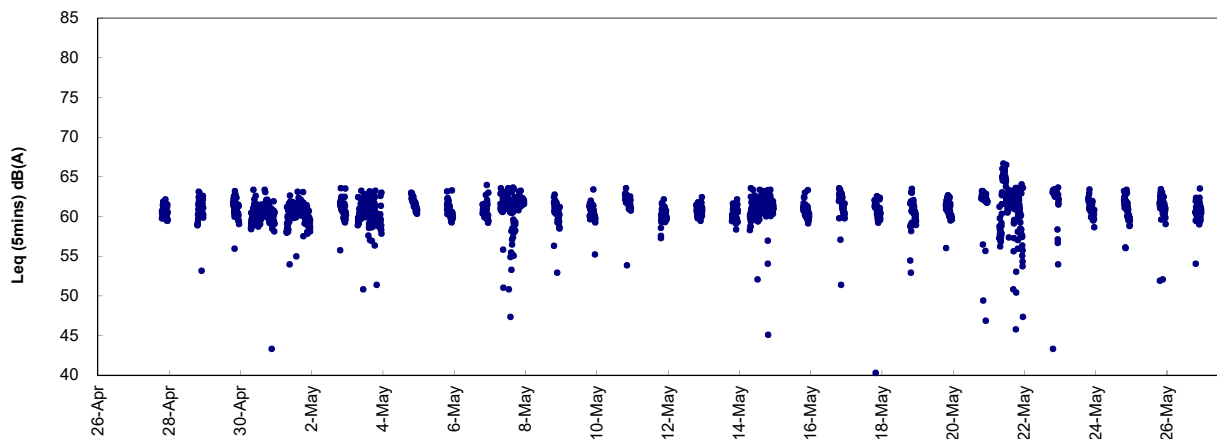
Sampling, Field Measurement and Testing Works (Stage 3)

Graphic Presentation of Real Time Noise Monitoring Result (RTN4-Causeway Bay Community Centre)


Day Time (0700 -1900 hrs on normal weekdays)



Restricted hours (1900 - 2300) on normal weekdays and 0700 - 2300 hrs on public holidays)



Night Time (2300 - 0700hrs)

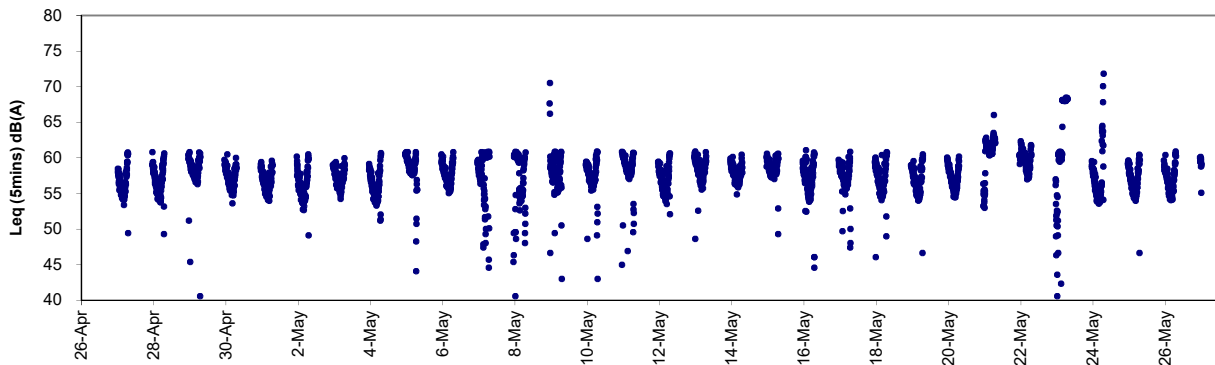



Appendix 4.3

Air Quality Monitoring Results and Graphical Presentations



Location: CMA1b - Oil Street Site Office

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 176.7

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
2-Mar-17	8:00	Fine	19471	2.8735	3.2476	9597.61	9621.61	24.00	1.48	1.48	1.48	2132	175.5
8-Mar-17	8:00	Rainy	19328	2.8503	2.9822	9624.63	9648.63	24.00	1.37	1.37	1.37	1968	67.0
14-Mar-17	8:00	Rainy	19644	2.8344	2.9779	9651.63	9675.63	24.00	1.36	1.37	1.36	1964	73.1
20-Mar-17	8:00	Cloudy	19702	2.8477	2.9705	9678.64	9702.64	24.00	1.36	1.35	1.35	1950	63.0
25-Mar-17	8:00	Cloudy	19594	2.8607	3.0031	9705.64	9729.64	24.00	1.36	1.37	1.37	1966	72.4

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 320.1

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Mar-17	8:50	Fine	19461	2.8944	2.9231	9621.61	9622.61	1.00	1.51	1.51	1.51	91	316.6
3-Mar-17	11:00	Fine	19338	2.8506	2.8688	9622.61	9623.61	1.00	1.37	1.37	1.37	82	222.1
3-Mar-17	13:00	Fine	19332	2.8384	2.8624	9623.61	9624.61	1.00	1.37	1.37	1.37	82	292.9
9-Mar-17	13:00	Cloudy	19659	2.8460	2.8578	9648.63	9649.63	1.00	1.31	1.31	1.31	78	150.4
9-Mar-17	15:05	Cloudy	19652	2.8284	2.8467	9649.63	9650.63	1.00	1.37	1.37	1.37	82	223.4
9-Mar-17	16:07	Cloudy	19648	2.8290	2.8417	9650.63	9651.63	1.00	1.37	1.37	1.37	82	155.0
15-Mar-17	9:10	Cloudy	19303	2.8560	2.8736	9675.63	9676.63	1.00	1.37	1.37	1.37	82	214.7
15-Mar-17	11:00	Cloudy	19300	2.8289	2.8403	9676.63	9677.63	1.00	1.37	1.37	1.37	82	139.0
15-Mar-17	15:05	Cloudy	19722	2.8367	2.8591	9677.63	9678.63	1.00	1.37	1.37	1.37	82	273.2
21-Mar-17	9:15	Cloudy	19290	2.8420	2.8517	9702.64	9703.64	1.00	1.35	1.35	1.35	81	119.5
21-Mar-17	10:35	Cloudy	19284	2.8624	2.8691	9703.64	9704.64	1.00	1.35	1.35	1.35	81	82.5
21-Mar-17	13:00	Cloudy	19611	2.8311	2.8371	9704.64	9705.64	1.00	1.35	1.35	1.35	81	73.9
27-Mar-17	9:15	Fine	19598	2.8626	2.8881	9729.64	9730.64	1.00	1.66	1.66	1.66	99	256.8
27-Mar-17	10:35	Fine	19566	2.8228	2.8755	9730.64	9731.64	1.00	1.54	1.54	1.54	92	570.6
27-Mar-17	13:25	Fine	19576	2.8618	2.8877	9731.64	9732.64	1.00	1.54	1.54	1.54	92	280.4



Location: CMA2a - Causeway Bay Community Centre

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 169.5

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
2-Mar-17	8:00	Fine	19472	2.8750	3.0462	19206.10	19230.10	24.00	1.14	1.14	1.14	1645	104.1
8-Mar-17	8:00	Rainy	19329	2.8692	2.9902	19233.10	19257.10	24.00	1.15	1.14	1.14	1648	73.4
14-Mar-17	8:00	Rainy	19646	2.8339	2.8868	19260.10	19284.10	24.00	1.14	1.14	1.14	1644	32.2
20-Mar-17	8:00	Cloudy	19703	2.8592	2.9107	19287.10	19311.10	24.00	1.13	1.13	1.13	1629	31.6
25-Mar-17	8:00	Cloudy	19592	2.8508	2.9208	19314.10	19338.10	24.00	1.14	1.15	1.14	1646	42.5

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 323.4

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Mar-17	8:30	Fine	19462	2.8729	2.8816	19230.10	19231.10	1.00	1.14	1.14	1.14	69	126.8
3-Mar-17	11:00	Fine	19339	2.8358	2.8497	19231.10	19232.10	1.00	1.14	1.14	1.14	69	202.6
3-Mar-17	13:00	Fine	19333	2.8458	2.8571	19232.10	19233.10	1.00	1.14	1.14	1.14	69	164.7
9-Mar-17	13:00	Cloudy	19657	2.8388	2.8502	19257.10	19258.10	1.00	1.14	1.14	1.14	69	166.2
9-Mar-17	15:02	Cloudy	19653	2.8456	2.8553	19258.10	19259.10	1.00	1.14	1.14	1.14	69	141.4
9-Mar-17	16:05	Cloudy	19649	2.8349	2.8438	19259.10	19260.10	1.00	1.14	1.14	1.14	69	129.8
15-Mar-17	9:05	Cloudy	19720	2.8702	2.8781	19284.10	19285.10	1.00	1.14	1.14	1.14	69	115.1
15-Mar-17	13:00	Cloudy	19716	2.8196	2.8283	19285.10	19286.10	1.00	1.21	1.21	1.21	73	119.7
15-Mar-17	15:05	Cloudy	19709	2.8318	2.8402	19286.10	19287.10	1.00	1.28	1.28	1.28	77	109.5
21-Mar-17	9:31	Cloudy	19292	2.8173	2.8237	19311.10	19312.10	1.00	1.13	1.13	1.13	68	94.4
21-Mar-17	10:51	Cloudy	19285	2.8410	2.8476	19312.10	19313.10	1.00	1.13	1.13	1.13	68	97.3
21-Mar-17	13:00	Cloudy	19612	2.8573	2.8619	19313.10	19314.10	1.00	1.13	1.13	1.13	68	67.8
27-Mar-17	9:25	Fine	19600	2.8601	2.8682	19338.10	19339.10	1.00	1.14	1.14	1.14	69	118.1
27-Mar-17	10:50	Fine	19817	2.7785	2.7872	19339.10	19340.10	1.00	1.14	1.14	1.14	69	126.8
27-Mar-17	13:30	Fine	19577	2.8184	2.8257	19340.10	19341.10	1.00	1.14	1.14	1.14	69	106.4



Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 171

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
2-Mar-17	8:00	Fine	19469	2.8717	3.0435	6684.45	6708.45	24.00	1.05	1.05	1.05	1508	113.9
8-Mar-17	8:00	Rainy	19330	2.8365	2.9659	6711.45	6735.45	24.00	1.09	1.08	1.09	1564	82.8
14-Mar-17	8:00	Rainy	19647	2.8490	2.8762	6738.45	6762.45	24.00	1.04	1.05	1.05	1507	18.1
20-Mar-17	8:00	Cloudy	19705	2.8404	2.9633	6765.46	6789.46	24.00	1.18	1.18	1.18	1697	72.4
25-Mar-17	8:00	Cloudy	19609	2.8485	2.9682	6792.46	6816.46	24.00	1.19	1.20	1.19	1717	69.7

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 311.3

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Mar-17	8:30	Fine	19463	2.8822	2.8950	6708.45	6709.45	1.00	1.19	1.19	1.19	72	178.8
3-Mar-17	10:30	Fine	19340	2.8466	2.8586	6709.45	6710.45	1.00	1.19	1.19	1.19	72	167.6
3-Mar-17	13:00	Fine	19334	2.8547	2.8663	6710.45	6711.45	1.00	1.19	1.19	1.19	72	162.1
9-Mar-17	13:00	Cloudy	19658	2.8400	2.8502	6735.45	6736.45	1.00	1.05	1.05	1.05	63	162.2
9-Mar-17	14:50	Cloudy	19654	2.8561	2.8622	6736.45	6737.45	1.00	1.05	1.05	1.05	63	97.0
9-Mar-17	15:55	Cloudy	19650	2.8328	2.8383	6737.45	6738.45	1.00	1.05	1.05	1.05	63	87.5
15-Mar-17	8:45	Cloudy	19304	2.8567	2.8766	6762.45	6763.45	1.00	1.19	1.19	1.19	72	277.8
15-Mar-17	10:50	Cloudy	19301	2.8413	2.8507	6763.45	6764.45	1.00	1.19	1.19	1.19	72	131.2
15-Mar-17	13:00	Cloudy	19707	2.8265	2.8356	6764.45	6765.45	1.00	1.19	1.19	1.19	72	127.1
21-Mar-17	8:50	Cloudy	19704	2.8517	2.8565	6789.46	6790.46	1.00	1.11	1.11	1.11	66	72.3
21-Mar-17	10:20	Cloudy	19287	2.8475	2.8519	6790.46	6791.46	1.00	1.11	1.11	1.11	66	66.3
21-Mar-17	13:00	Cloudy	19278	2.8493	2.8531	6791.46	6792.46	1.00	1.18	1.18	1.18	71	53.8
27-Mar-17	8:45	Fine	19597	2.8420	2.8535	6816.46	6817.46	1.00	1.19	1.19	1.19	72	160.7
27-Mar-17	10:05	Fine	19815	2.8376	2.8510	6817.46	6818.46	1.00	1.19	1.19	1.19	72	187.3
27-Mar-17	13:00	Fine	19819	2.7936	2.8039	6818.46	6819.46	1.00	1.19	1.19	1.19	72	143.9



Location: CMA4a - SPCA

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 171.2

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
2-Mar-17	8:00	Fine	19470	2.8840	3.0916	23444.51	23468.51	24.00	1.23	1.24	1.23	1778	116.7
8-Mar-17	8:00	Rainy	19331	2.8440	2.9894	23471.51	23495.51	24.00	1.24	1.24	1.24	1781	81.6
14-Mar-17	8:00	Rainy	19645	2.8301	2.9192	23498.80	23522.80	24.00	1.23	1.24	1.23	1778	50.1
20-Mar-17	8:00	Cloudy	19706	2.8349	2.9312	23525.81	23549.81	24.00	1.28	1.27	1.27	1836	52.5
25-Mar-17	8:00	Cloudy	19610	2.8423	3.0111	23552.81	23576.81	24.00	1.28	1.29	1.28	1850	91.3

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 312.5

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Mar-17	8:20	Fine	19464	2.8870	2.8976	23468.51	23469.51	1.00	1.19	1.19	1.19	71	148.8
3-Mar-17	10:30	Fine	19341	2.8448	2.8618	23469.51	23470.51	1.00	1.24	1.24	1.24	74	229.2
3-Mar-17	13:00	Fine	19335	2.8401	2.9098	23470.51	23471.51	1.00	1.24	1.24	1.24	74	939.9
9-Mar-17	13:00	Cloudy	19656	2.8330	2.8446	23495.51	23496.51	1.00	1.24	1.24	1.24	74	156.5
9-Mar-17	14:46	Cloudy	19655	2.8200	2.8305	23496.51	23497.51	1.00	1.24	1.24	1.24	74	141.6
9-Mar-17	15:50	Cloudy	19651	2.8279	2.8370	23497.51	23498.51	1.00	1.19	1.19	1.19	71	127.8
15-Mar-17	8:05	Cloudy	19721	2.8386	2.8449	23522.80	23523.80	1.00	1.24	1.24	1.24	74	84.9
15-Mar-17	10:10	Cloudy	19717	2.8269	2.8335	23523.80	23524.80	1.00	1.19	1.19	1.19	71	92.6
15-Mar-17	15:50	Cloudy	19708	2.8324	2.8424	23524.80	23525.80	1.00	1.24	1.24	1.24	74	134.8
21-Mar-17	9:05	Cloudy	19295	2.8581	2.8616	23549.81	23550.81	1.00	1.18	1.18	1.18	71	49.5
21-Mar-17	10:35	Cloudy	19288	2.8286	2.8326	23550.81	23551.81	1.00	1.18	1.18	1.18	71	56.6
21-Mar-17	13:00	Cloudy	19279	2.8309	2.8336	23551.81	23552.81	1.00	1.18	1.18	1.18	71	38.2
27-Mar-17	9:00	Fine	19596	2.8451	2.8544	23589.09	23590.09	1.00	1.28	1.28	1.28	77	120.7
27-Mar-17	10:06	Fine	19567	2.8081	2.8200	23590.09	23591.09	1.00	1.28	1.28	1.28	77	154.4
27-Mar-17	13:00	Fine	19578	2.8331	2.8432	23591.09	23592.09	1.00	1.28	1.28	1.28	77	131.0



Location: CMA5b - Pedestrian Plaza

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 181

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
2-Mar-17	8:00	Fine	19475	2.8863	3.2871	8051.77	8075.77	24.00	0.97	0.97	0.97	1395	287.3
8-Mar-17	8:00	Rainy	19395	2.8372	3.0238	8078.77	8102.77	24.00	0.97	0.97	0.97	1398	133.4
14-Mar-17	8:00	Rainy	18502	2.8180	2.9047	8105.77	8129.77	24.00	0.85	0.85	0.85	1225	70.8
20-Mar-17	8:00	Cloudy	18496	2.8166	3.0109	8132.77	8156.77	24.00	0.96	0.96	0.96	1380	140.8
25-Mar-17	8:00	Cloudy	19283	2.8364	3.0069	8159.77	8183.77	24.00	0.91	0.92	0.91	1311	130.0

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 332

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Mar-17	8:02	Fine	19537	2.8406	2.8635	8075.77	8076.77	1.00	1.09	1.15	1.12	67	341.6
3-Mar-17	9:30	Fine	19460	2.8701	2.8879	8076.77	8077.77	1.00	0.85	0.85	0.85	51	348.1
3-Mar-17	13:00	Fine	19337	2.8264	2.8745	8077.77	8078.77	1.00	0.97	0.97	0.97	58	826.4
9-Mar-17	9:30	Cloudy	18510	2.8400	2.8579	8102.77	8103.77	1.00	0.97	0.97	0.97	58	307.7
9-Mar-17	10:40	Cloudy	18507	2.8049	2.8254	8103.77	8104.77	1.00	1.09	1.09	1.09	65	314.3
9-Mar-17	13:00	Cloudy	18505	2.8040	2.8083	8104.77	8105.77	1.00	0.85	0.85	0.85	51	84.1
15-Mar-17	8:30	Cloudy	18513	2.8218	2.8319	8129.77	8130.77	1.00	0.97	0.97	0.97	58	173.4
15-Mar-17	9:38	Cloudy	19719	2.8359	2.8450	8130.77	8131.77	1.00	0.97	0.97	0.97	58	156.3
15-Mar-17	13:00	Cloudy	19715	2.8084	2.8257	8131.77	8132.77	1.00	0.97	0.97	0.97	58	297.0
21-Mar-17	8:30	Cloudy	19293	2.8433	2.8516	8156.77	8157.77	1.00	0.84	0.84	0.84	50	164.6
21-Mar-17	9:38	Cloudy	19289	2.8416	2.8515	8157.77	8158.77	1.00	0.96	0.96	0.96	57	172.4
21-Mar-17	13:00	Cloudy	19282	2.8482	2.8570	8158.77	8159.77	1.00	0.96	0.96	0.96	57	153.2
27-Mar-17	8:03	Fine	19602	2.8572	2.8677	8183.77	8184.77	1.00	0.85	0.85	0.85	51	205.4
27-Mar-17	9:45	Fine	19568	2.8204	2.8290	8184.77	8185.77	1.00	0.85	0.85	0.85	51	168.2
27-Mar-17	13:00	Fine	19816	2.8006	2.8178	8185.77	8186.77	1.00	0.85	0.88	0.87	52	330.7

Location: MA1e - International Finance Centre (Eastern Wing)

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 173.4

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
2-Mar-17	8:00	Fine	19496	2.8851	3.0867	20389.46	20413.46	24.00	1.22	1.22	1.22	1753	115.0
8-Mar-17	8:00	Rainy	19316	2.8355	2.9465	20416.46	20440.46	24.00	1.22	1.22	1.22	1756	63.2
14-Mar-17	8:00	Rainy	18606	2.7999	2.8741	20443.46	20467.46	24.00	1.21	1.22	1.22	1752	42.4
20-Mar-17	8:00	Cloudy	19726	2.8161	2.9144	20470.46	20494.46	24.00	1.21	1.21	1.21	1738	56.6
25-Mar-17	8:00	Cloudy	19688	2.8512	2.9614	20497.46	20521.46	24.00	1.21	1.22	1.22	1754	62.8

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 325.1

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Mar-17	8:03	Fine	19322	2.8644	2.8745	20413.46	20414.46	1.00	1.22	1.22	1.22	73	138.2
3-Mar-17	9:05	Fine	19319	2.8639	2.8717	20414.46	20415.46	1.00	1.22	1.22	1.22	73	106.7
3-Mar-17	10:08	Fine	19319	2.8362	2.8426	20415.46	20416.46	1.00	1.22	1.22	1.22	73	87.5
9-Mar-17	8:18	Cloudy	19127	2.8017	2.8072	20440.46	20441.46	1.00	1.22	1.22	1.22	73	75.3
9-Mar-17	9:21	Cloudy	19124	2.8686	2.8744	20441.46	20442.46	1.00	1.22	1.22	1.22	73	79.4
9-Mar-17	11:00	Cloudy	19124	2.8356	2.8427	20442.46	20443.46	1.00	1.22	1.22	1.22	73	97.2
15-Mar-17	8:05	Cloudy	19732	2.8097	2.8124	20467.46	20468.46	1.00	1.10	1.10	1.10	66	40.7
15-Mar-17	9:10	Cloudy	19729	2.8179	2.8206	20468.46	20469.46	1.00	1.22	1.22	1.22	73	36.9
15-Mar-17	11:00	Cloudy	19729	2.8385	2.8426	20469.46	20470.46	1.00	1.22	1.22	1.22	73	56.1
21-Mar-17	8:02	Cloudy	19694	2.8292	2.8312	20494.46	20495.46	1.00	1.21	1.21	1.21	72	27.6
21-Mar-17	9:05	Cloudy	19691	2.8388	2.8424	20495.46	20496.46	1.00	1.21	1.21	1.21	72	49.8
21-Mar-17	10:07	Cloudy	19691	2.8240	2.8294	20496.46	20497.46	1.00	1.21	1.21	1.21	72	74.6
27-Mar-17	8:02	Fine	19587	2.8401	2.8450	20521.46	20522.46	1.00	1.22	1.22	1.22	73	67.0
27-Mar-17	9:05	Fine	19584	2.8273	2.8341	20522.46	20523.46	1.00	1.22	1.22	1.22	73	93.0
27-Mar-17	10:07	Fine	19584	2.8599	2.8677	20523.46	20524.46	1.00	1.22	1.22	1.22	73	106.7



Location: MA1w - International Finance Centre (Western Wing)

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 173.4
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
2-Mar-17	8:00	Fine	19495	2.8858	3.0733	20170.69	20194.69	24.00	1.35	1.35	1.35	1944	96.4
8-Mar-17	8:00	Rainy	19315	2.8310	2.9391	20197.69	20221.69	24.00	1.35	1.35	1.35	1947	55.5
14-Mar-17	8:00	Rainy	18607	2.7874	2.8666	20224.69	20248.69	24.00	1.35	1.35	1.35	1943	40.8
20-Mar-17	8:00	Cloudy	19725	2.8276	2.9160	20251.69	20275.69	24.00	1.34	1.34	1.34	1931	45.8
25-Mar-17	8:00	Cloudy	19687	2.8488	2.9482	20278.69	20302.69	24.00	1.35	1.36	1.35	1945	51.1

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 325.1
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
3-Mar-17	8:05	Fine	19324	2.8604	2.8684	20194.69	20195.69	1.00	1.35	1.35	1.35	81	98.7
3-Mar-17	9:07	Fine	19321	2.8605	2.8663	20195.69	20196.69	1.00	1.35	1.35	1.35	81	71.5
3-Mar-17	10:09	Fine	19318	2.8533	2.8632	20196.69	20197.69	1.00	1.35	1.35	1.35	81	122.1
9-Mar-17	8:15	Cloudy	18525	2.8174	2.8223	20221.69	20222.69	1.00	1.35	1.35	1.35	81	60.5
9-Mar-17	9:19	Cloudy	19128	2.8534	2.8604	20222.69	20223.69	1.00	1.35	1.35	1.35	81	86.4
9-Mar-17	11:00	Cloudy	19125	2.8407	2.8471	20223.69	20224.69	1.00	1.35	1.35	1.35	81	79.0
15-Mar-17	8:07	Cloudy	19734	2.8499	2.8550	20248.69	20249.69	1.00	1.35	1.35	1.35	81	62.9
15-Mar-17	9:11	Cloudy	19731	2.8317	2.8360	20249.69	20250.69	1.00	1.35	1.35	1.35	81	53.0
15-Mar-17	10:16	Cloudy	19728	2.8313	2.8362	20250.69	20251.69	1.00	1.35	1.35	1.35	81	60.4
21-Mar-17	8:02	Cloudy	19695	2.8224	2.8249	20275.69	20276.69	1.00	1.34	1.34	1.34	80	31.1
21-Mar-17	9:05	Cloudy	19693	2.8302	2.8337	20276.69	20277.69	1.00	1.34	1.34	1.34	80	43.5
21-Mar-17	10:09	Cloudy	19690	2.8163	2.8219	20277.69	20278.69	1.00	1.34	1.34	1.34	80	69.6
27-Mar-17	8:05	Fine	19589	2.8459	2.8515	20302.69	20303.69	1.00	1.35	1.35	1.35	81	69.1
27-Mar-17	9:07	Fine	19586	2.8609	2.8666	20303.69	20304.69	1.00	1.35	1.35	1.35	81	70.3
27-Mar-17	10:09	Fine	19583	2.8377	2.8417	20304.69	20305.69	1.00	1.35	1.35	1.35	81	49.3



Location: CMA1b - Oil Street Site Office

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 176.7

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
31-Mar-17	8:00	Rainy	19820	2.8288	2.9358	9732.64	9756.64	24.00	1.36	1.36	1.36	1960	54.6
6-Apr-17	8:00	Fine	19895	2.6424	2.8509	9759.80	9783.80	24.00	1.35	1.35	1.35	1942	107.3
12-Apr-17	8:00	Rainy	19879	2.6512	2.7707	9786.80	9810.80	24.00	1.36	1.36	1.36	1955	61.1
18-Apr-17	8:00	Fine	20050	2.5123	2.6409	9813.84	9837.84	24.00	1.18	1.18	1.18	1702	75.6
24-Apr-17	8:00	Cloudy	20135	2.5640	2.7350	9840.84	9864.84	24.00	1.08	1.08	1.08	1556	109.9

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 320.1

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
1-Apr-17	8:50	Cloudy	19811	2.8227	2.8371	9756.64	9757.64	1.00	1.36	1.36	1.36	82	176.0
1-Apr-17	10:15	Cloudy	19805	2.8052	2.8180	9757.64	9758.64	1.00	1.36	1.36	1.36	82	156.4
1-Apr-17	13:00	Cloudy	19780	2.8344	2.8403	9758.64	9759.64	1.00	1.36	1.36	1.36	82	72.1
7-Apr-17	9:00	Fine	19894	2.6410	2.6546	9783.80	9784.80	1.00	1.35	1.35	1.35	81	168.2
7-Apr-17	10:40	Fine	19884	2.6488	2.6569	9784.80	9785.80	1.00	1.35	1.35	1.35	81	100.2
7-Apr-17	13:00	Fine	19881	2.6342	2.6418	9785.80	9786.80	1.00	1.35	1.35	1.35	81	94.0
13-Apr-17	8:50	Cloudy	19851	2.6411	2.6520	9810.80	9811.80	1.00	1.36	1.36	1.36	82	133.6
13-Apr-17	10:20	Cloudy	19855	2.6384	2.6470	9811.80	9812.80	1.00	1.36	1.36	1.36	82	105.4
13-Apr-17	13:00	Cloudy	19618	2.8393	2.8469	9812.80	9813.80	1.00	1.20	1.20	1.20	72	105.6
19-Apr-17	8:50	Fine	20043	2.4815	2.4869	9837.84	9838.84	1.00	1.18	1.18	1.18	71	76.2
19-Apr-17	10:30	Fine	20085	2.4943	2.5018	9838.84	9839.84	1.00	1.18	1.18	1.18	71	105.8
19-Apr-17	13:00	Fine	20078	2.4763	2.4862	9839.84	9840.84	1.00	1.18	1.18	1.18	71	139.6
25-Apr-17	9:00	Cloudy	20142	2.5916	2.6070	9864.84	9865.84	1.00	1.22	1.22	1.22	73	210.2
25-Apr-17	10:35	Cloudy	20151	2.5686	2.5843	9865.84	9866.84	1.00	1.22	1.22	1.22	73	214.3
25-Apr-17	13:00	Cloudy	20146	2.5758	2.5987	9866.84	9867.84	1.00	1.22	1.22	1.22	73	312.6



Location: CMA2a - Causeway Bay Community Centre

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 169.5

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
31-Mar-17	8:00	Rainy	19574	2.8298	2.8807	19342.10	19366.10	24.00	1.14	1.14	1.14	1640	31.0
6-Apr-17	8:00	Fine	19776	2.8193	2.9262	19369.10	19393.10	24.00	1.13	1.12	1.13	1621	65.9
12-Apr-17	8:00	Rainy	19880	2.6569	2.7438	19396.10	19420.10	24.00	1.27	1.27	1.27	1827	47.6
18-Apr-17	8:00	Fine	20051	2.5074	2.6344	19423.14	19447.14	24.00	1.03	1.03	1.03	1482	85.7
24-Apr-17	8:00	Cloudy	20074	2.5135	2.6729	19450.14	19474.14	24.00	1.08	1.08	1.08	1556	102.5

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 323.4

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
1-Apr-17	8:50	Cloudy	19812	2.8221	2.8259	19366.10	19367.10	1.00	1.14	1.14	1.14	68	55.5
1-Apr-17	10:00	Cloudy	19806	2.7981	2.8007	19367.10	19368.10	1.00	1.14	1.14	1.14	68	38.0
1-Apr-17	13:00	Cloudy	19781	2.8283	2.8322	19368.10	19369.10	1.00	1.14	1.14	1.14	68	56.9
7-Apr-17	9:05	Fine	20001	2.8294	2.8334	19393.10	19394.10	1.00	1.12	1.12	1.12	67	59.3
7-Apr-17	10:40	Fine	19888	2.6375	2.6428	19394.10	19395.10	1.00	1.12	1.12	1.12	67	78.5
7-Apr-17	13:15	Fine	19882	2.6732	2.6779	19395.10	19396.10	1.00	1.12	1.12	1.12	67	69.6
13-Apr-17	9:30	Cloudy	19850	2.6174	2.6215	19420.10	19421.10	1.00	1.14	1.14	1.14	68	60.1
13-Apr-17	10:32	Cloudy	19856	2.6350	2.6402	19421.10	19422.10	1.00	1.14	1.14	1.14	68	76.2
13-Apr-17	13:00	Cloudy	19619	2.8314	2.8366	19422.10	19423.10	1.00	0.98	0.98	0.98	59	88.7
19-Apr-17	9:10	Fine	20045	2.4950	2.5046	19447.14	19448.14	1.00	1.10	1.10	1.10	66	145.2
19-Apr-17	10:40	Fine	20071	2.4790	2.4852	19448.14	19449.14	1.00	0.99	0.99	0.99	60	104.0
19-Apr-17	13:00	Fine	20079	2.4795	2.4833	19449.14	19450.14	1.00	0.96	0.96	0.96	57	66.2
25-Apr-17	9:20	Cloudy	20141	2.5642	2.5733	19474.15	19475.15	1.00	0.97	0.97	0.97	58	156.4
25-Apr-17	10:45	Cloudy	20153	2.5854	2.5916	19475.15	19476.15	1.00	0.97	0.97	0.97	58	106.6
25-Apr-17	13:00	Cloudy	20145	2.5442	2.5507	19476.15	19477.15	1.00	1.04	1.04	1.04	63	103.9



Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 171

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
31-Mar-17	8:00	Rainy	19822	2.6356	2.7118	6819.48	6843.48	24.00	1.18	1.19	1.19	1710	44.6
7-Apr-17	17:10	Fine	19875	2.6320	2.7301	6862.64	6886.64	24.00	1.17	1.17	1.17	1685	58.2
12-Apr-17	8:00	Rainy	19871	2.6566	2.7168	6886.64	6910.64	24.00	1.18	1.19	1.18	1704	35.3
18-Apr-17	8:00	Fine	20052	2.5142	2.6590	6913.64	6937.64	24.00	1.16	1.16	1.16	1676	86.4
24-Apr-17	8:00	Cloudy	20162	2.5782	2.6857	6940.65	6964.65	24.00	1.02	1.02	1.02	1472	73.0

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 6 April 2017 to 7 April 2017.

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 311.3

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
1-Apr-17	8:30	Cloudy	19813	2.8067	2.8094	6843.48	6844.48	1.00	1.19	1.19	1.19	71	37.8
1-Apr-17	9:55	Cloudy	19807	2.8197	2.8230	6844.48	6845.48	1.00	1.19	1.19	1.19	71	46.2
1-Apr-17	11:00	Cloudy	19803	2.8094	2.8123	6845.48	6846.48	1.00	1.19	1.19	1.19	71	40.6
7-Apr-17	14:00	Fine	20000	2.8479	2.8531	6859.64	6860.64	1.00	1.03	1.03	1.03	62	84.3
7-Apr-17	15:02	Fine	19878	2.6293	2.6343	6860.64	6861.64	1.00	1.03	1.03	1.03	62	81.0
7-Apr-17	16:05	Fine	19889	2.6422	2.6462	6861.64	6862.64	1.00	1.10	1.10	1.10	66	60.6
13-Apr-17	8:03	Cloudy	19867	2.6305	2.6340	6910.64	6911.64	1.00	1.19	1.19	1.19	71	49.2
13-Apr-17	10:00	Cloudy	19853	2.6398	2.6433	6911.64	6912.64	1.00	1.19	1.19	1.19	71	49.2
13-Apr-17	13:00	Cloudy	19223	2.8483	2.8529	6912.64	6913.64	1.00	1.19	1.19	1.19	71	64.7
19-Apr-17	8:30	Fine	20047	2.5189	2.5204	6937.64	6938.64	1.00	1.02	1.02	1.02	61	24.5
19-Apr-17	10:15	Fine	20069	2.4700	2.4727	6938.64	6939.64	1.00	1.02	1.02	1.02	61	44.0
19-Apr-17	13:00	Fine	20081	2.4959	2.4992	6939.64	6940.64	1.00	1.02	1.02	1.02	61	53.8
25-Apr-17	8:40	Cloudy	20139	2.5272	2.5348	6964.65	6965.65	1.00	1.16	1.16	1.16	69	109.5
25-Apr-17	10:15	Cloudy	20155	2.5442	2.5510	6965.65	6966.65	1.00	1.16	1.16	1.16	69	98.0
25-Apr-17	13:00	Cloudy	20147	2.5923	2.5995	6966.65	6967.65	1.00	1.16	1.16	1.16	69	103.8



Location: CMA4a - SPCA

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 171.2

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
31-Mar-17	8:00	Rainy	19575	2.8523	2.8974	23592.09	23616.09	24.00	1.23	1.23	1.23	1775	25.4
7-Apr-17	14:45	Fine	19872	2.6509	2.7338	23622.09	23646.09	24.00	1.27	1.27	1.27	1828	45.3
12-Apr-17	8:00	Rainy	19870	2.6412	2.6942	23646.14	23670.14	24.00	1.28	1.28	1.28	1840	28.8
18-Apr-17	8:00	Fine	20042	2.4916	2.5760	23673.14	23697.14	24.00	1.26	1.26	1.26	1821	46.3
24-Apr-17	8:00	Cloudy	20073	2.4700	2.6078	23700.15	23724.15	24.00	0.93	0.93	0.93	1334	103.3

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 6 April 2017 to 7 April 2017.

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 312.5

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
1-Apr-17	8:30	Cloudy	19798	2.8112	2.8124	23616.09	23617.09	1.00	1.28	1.28	1.28	77	15.6
1-Apr-17	9:55	Cloudy	19808	2.8094	2.8123	23617.09	23618.09	1.00	1.28	1.28	1.28	77	37.7
1-Apr-17	11:00	Cloudy	19802	2.8182	2.8199	23618.09	23619.09	1.00	1.28	1.28	1.28	77	22.1
7-Apr-17	8:40	Fine	19999	2.8477	2.8518	23619.09	23620.09	1.00	1.27	1.27	1.27	76	53.8
7-Apr-17	10:10	Fine	19890	2.6440	2.6462	23620.09	23621.09	1.00	1.22	1.22	1.22	73	30.0
7-Apr-17	13:00	Fine	19887	2.6249	2.6295	23621.09	23622.09	1.00	1.27	1.27	1.27	76	60.4
13-Apr-17	8:45	Cloudy	19849	2.6558	2.6585	23670.14	23671.14	1.00	1.28	1.28	1.28	77	35.2
13-Apr-17	10:00	Cloudy	19857	2.6414	2.6433	23671.14	23672.14	1.00	1.28	1.28	1.28	77	24.7
13-Apr-17	13:00	Cloudy	19617	2.8563	2.8605	23672.14	23673.14	1.00	1.28	1.28	1.28	77	54.7
19-Apr-17	8:30	Fine	20048	2.5077	2.5114	23697.15	23698.15	1.00	1.26	1.26	1.26	76	48.8
19-Apr-17	10:15	Fine	20068	2.5062	2.5091	23698.15	23699.15	1.00	1.26	1.26	1.26	76	38.2
19-Apr-17	13:00	Fine	20082	2.4673	2.4697	23699.15	23700.15	1.00	1.26	1.26	1.26	76	31.6
25-Apr-17	8:50	Cloudy	20138	2.5743	2.5808	23724.15	23725.15	1.00	0.93	0.93	0.93	56	117.0
25-Apr-17	10:15	Cloudy	20156	2.5620	2.5681	23725.15	23726.15	1.00	0.93	0.93	0.93	56	109.8
25-Apr-17	13:00	Cloudy	20148	2.5513	2.5586	23726.15	23727.15	1.00	0.93	0.93	0.93	56	131.4



Location: CMA5b - Pedestrian Plaza

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 181

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
31-Mar-17	8:00	Rainy	19823	2.6104	2.6631	8187.71	8211.71	24.00	0.85	0.85	0.85	1221	43.2
6-Apr-17	8:00	Fine	19779	2.8292	2.9819	8214.71	8238.71	24.00	0.84	0.84	0.84	1205	126.7
12-Apr-17	8:00	Rainy	19877	2.6223	2.7310	8241.71	8265.71	24.00	0.90	0.91	0.90	1301	83.5
18-Apr-17	8:00	Fine	19972	2.9208	3.0670	8268.71	8292.71	24.00	0.83	0.83	0.83	1196	122.2
24-Apr-17	8:00	Cloudy	20077	2.4703	2.6024	8295.71	8319.71	24.00	0.89	0.89	0.89	1282	103.0

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 332

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
1-Apr-17	8:03	Cloudy	19821	2.6456	2.6568	8211.71	8212.71	1.00	0.91	0.91	0.91	55	205.3
1-Apr-17	9:35	Cloudy	19799	2.8229	2.8336	8212.71	8213.71	1.00	0.91	0.91	0.91	55	196.2
1-Apr-17	10:45	Cloudy	19804	2.7975	2.8064	8213.71	8214.71	1.00	0.91	0.91	0.91	55	163.2
7-Apr-17	8:15	Fine	19996	2.8489	2.8581	8238.71	8239.71	1.00	0.84	0.86	0.85	51	180.4
7-Apr-17	9:35	Fine	19893	2.6444	2.6496	8239.71	8240.71	1.00	0.84	0.84	0.84	50	103.7
7-Apr-17	11:00	Fine	19885	2.6526	2.6649	8240.71	8241.71	1.00	0.89	0.89	0.89	54	229.4
13-Apr-17	8:10	Cloudy	19848	2.6621	2.6671	8265.71	8266.71	1.00	0.96	0.96	0.96	58	86.4
13-Apr-17	9:40	Cloudy	19852	2.6378	2.6448	8266.71	8267.71	1.00	0.96	0.96	0.96	58	121.0
13-Apr-17	11:00	Cloudy	19595	2.8511	2.8625	8267.71	8268.71	1.00	0.96	0.96	0.96	58	197.1
19-Apr-17	8:05	Fine	20167	2.5751	2.5824	8292.71	8293.71	1.00	0.89	0.89	0.89	53	137.0
19-Apr-17	9:50	Fine	20044	2.5039	2.5057	8293.71	8294.71	1.00	0.83	0.83	0.83	50	36.1
19-Apr-17	13:00	Fine	20072	2.4903	2.4936	8294.71	8295.71	1.00	0.89	0.89	0.89	53	61.9
25-Apr-17	8:25	Cloudy	20137	2.5387	2.5453	8319.75	8320.75	1.00	0.76	0.76	0.76	46	143.8
25-Apr-17	9:55	Cloudy	20143	2.5594	2.5712	8320.75	8321.75	1.00	0.76	0.76	0.76	46	257.2
25-Apr-17	11:00	Cloudy	20152	2.5829	2.5960	8321.75	8322.75	1.00	0.76	0.76	0.76	46	285.5

Location: MA1e - International Finance Centre (Eastern Wing)

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 173.4

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
31-Mar-17	8:00	Rainy	19582	2.8528	3.0064	20524.46	20548.46	24.00	1.21	1.22	1.21	1748	87.9
6-Apr-17	8:00	Fine	19795	2.8149	2.9222	20551.46	20575.46	24.00	1.20	1.20	1.20	1730	62.0
12-Apr-17	8:00	Rainy	19966	2.8351	2.8825	20578.46	20602.46	24.00	1.18	1.18	1.18	1702	27.8
18-Apr-17	8:00	Fine	20126	2.6240	2.7717	20605.46	20629.46	24.00	1.20	1.20	1.20	1721	85.8
24-Apr-17	8:00	Cloudy	19977	2.9188	3.0550	20632.46	20656.46	24.00	1.10	1.10	1.10	1583	86.0

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 325.1

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
1-Apr-17	8:46	Cloudy	19786	2.8208	2.8236	20548.46	20549.46	1.00	1.22	1.22	1.22	73	38.4
1-Apr-17	9:48	Cloudy	19789	2.8092	2.8106	20549.46	20550.46	1.00	1.22	1.22	1.22	73	19.2
1-Apr-17	10:50	Cloudy	19789	2.8224	2.8239	20550.46	20551.46	1.00	1.22	1.22	1.22	73	20.6
7-Apr-17	9:15	Fine	19968	2.8375	2.8401	20575.46	20576.46	1.00	1.09	1.09	1.09	65	39.8
7-Apr-17	10:17	Fine	19967	2.8529	2.8557	20576.46	20577.46	1.00	1.09	1.09	1.09	65	42.9
7-Apr-17	13:00	Fine	19967	2.8380	2.8423	20577.46	20578.46	1.00	1.20	1.20	1.20	72	59.7
13-Apr-17	9:30	Cloudy	19792	2.8409	2.8445	20602.46	20603.46	1.00	1.21	1.21	1.21	73	49.5
13-Apr-17	10:31	Cloudy	19794	2.8224	2.8251	20603.46	20604.46	1.00	1.21	1.21	1.21	73	37.1
13-Apr-17	13:00	Cloudy	19793	2.8419	2.8456	20604.46	20605.46	1.00	1.21	1.21	1.21	73	50.9
19-Apr-17	9:50	Fine	19983	2.8504	2.8536	20629.46	20630.46	1.00	1.20	1.20	1.20	72	44.6
19-Apr-17	13:00	Fine	18495	2.8304	2.8317	20630.46	20631.46	1.00	1.08	1.08	1.08	65	20.0
19-Apr-17	14:02	Fine	19979	2.8986	2.9006	20631.46	20632.46	1.00	1.20	1.20	1.20	72	27.9
25-Apr-17	9:45	Cloudy	20067	2.4936	2.5011	20656.53	20657.53	1.00	1.10	1.10	1.10	66	113.7
25-Apr-17	10:47	Cloudy	20066	2.5056	2.5117	20657.53	20658.53	1.00	1.10	1.10	1.10	66	92.5
25-Apr-17	13:00	Cloudy	20065	2.5092	2.5163	20658.53	20659.53	1.00	1.10	1.10	1.10	66	107.7



Location: MA1w - International Finance Centre (Western Wing)

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 173.4
Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
31-Mar-17	8:00	Rainy	19581	2.8661	2.8954	20305.69	20329.69	24.00	1.35	1.35	1.35	1940	15.1
6-Apr-17	8:00	Fine	19796	2.8156	2.9114	20332.69	20356.69	24.00	1.34	1.34	1.34	1924	49.8
12-Apr-17	8:00	Rainy	19960	2.8397	2.8946	20359.69	20383.69	24.00	1.34	1.35	1.34	1936	28.4
18-Apr-17	8:00	Fine	20125	2.5511	2.6693	20386.69	20410.69	24.00	1.33	1.33	1.33	1916	61.7
24-Apr-17	8:00	Cloudy	19976	2.9336	3.0773	20413.69	20437.69	24.00	1.32	1.32	1.32	1896	75.8

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 325.1
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
1-Apr-17	8:47	Cloudy	19784	2.8245	2.8265	20329.69	20330.69	1.00	1.35	1.35	1.35	81	24.7
1-Apr-17	9:49	Cloudy	19787	2.7974	2.7989	20330.69	20331.69	1.00	1.35	1.35	1.35	81	18.5
1-Apr-17	10:52	Cloudy	19790	2.8286	2.8297	20331.69	20332.69	1.00	1.35	1.35	1.35	81	13.6
7-Apr-17	9:18	Fine	19957	2.8293	2.8330	20356.69	20357.69	1.00	1.34	1.34	1.34	80	46.2
7-Apr-17	10:24	Fine	19956	2.8458	2.8497	20357.69	20358.69	1.00	1.34	1.34	1.34	80	48.7
7-Apr-17	13:00	Fine	19961	2.8512	2.8542	20358.69	20359.69	1.00	1.34	1.34	1.34	80	37.4
13-Apr-17	9:33	Cloudy	20122	2.5713	2.5731	20383.69	20384.69	1.00	1.35	1.35	1.35	81	22.3
13-Apr-17	10:35	Cloudy	20123	2.5645	2.5667	20384.69	20385.69	1.00	1.35	1.35	1.35	81	27.2
13-Apr-17	13:00	Cloudy	20124	2.5869	2.5899	20385.69	20386.69	1.00	1.35	1.35	1.35	81	37.1
19-Apr-17	9:57	Fine	19982	2.8435	2.8470	20410.69	20411.69	1.00	1.33	1.33	1.33	80	43.8
19-Apr-17	13:00	Fine	18518	2.8391	2.8427	20411.69	20412.69	1.00	1.33	1.33	1.33	80	45.1
19-Apr-17	14:05	Fine	19978	2.8970	2.8993	20412.69	20413.69	1.00	1.33	1.33	1.33	80	28.8
25-Apr-17	9:46	Cloudy	20063	2.5071	2.5164	20437.83	20438.83	1.00	1.32	1.32	1.32	79	117.8
25-Apr-17	10:48	Cloudy	20062	2.4971	2.5066	20438.83	20439.83	1.00	1.32	1.32	1.32	79	120.3
25-Apr-17	13:00	Cloudy	20061	2.4790	2.4877	20439.83	20440.83	1.00	1.32	1.32	1.32	79	110.2



Location: CMA1b - Oil Street Site Office

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 176.7

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
28-Apr-17	8:00	Fine	20179	2.5737	2.7272	9867.84	9891.84	24.00	1.14	1.14	1.14	1637	93.8
4-May-17	8:00	Rainy	20281	2.5669	2.6705	9894.86	9918.86	24.00	1.19	1.19	1.19	1709	60.6
10-May-17	8:00	Fine	20364	2.9426	3.1379	9921.87	9945.87	24.00	1.13	1.13	1.13	1624	120.2
16-May-17	8:00	Cloudy	20420	2.8407	2.9583	9948.87	9972.87	24.00	1.18	1.18	1.18	1706	68.9
22-May-17	8:00	Cloudy	20403	2.8484	2.9709	9975.87	9999.87	24.00	1.18	1.18	1.18	1705	71.9

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 320.1

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Apr-17	8:45	Fine	20174	2.5705	2.5843	9891.84	9892.84	1.00	1.19	1.19	1.19	72	193.0
29-Apr-17	9:58	Fine	20295	2.5510	2.5669	9892.84	9893.84	1.00	1.19	1.19	1.19	72	222.3
29-Apr-17	11:00	Fine	20288	2.5763	2.5867	9893.84	9894.84	1.00	1.19	1.19	1.19	72	145.4
5-May-17	9:30	Fine	20328	2.8960	2.9045	9918.87	9919.87	1.00	1.19	1.19	1.19	71	119.4
5-May-17	11:00	Fine	20251	2.5800	2.5876	9919.87	9920.87	1.00	1.19	1.19	1.19	71	106.8
5-May-17	15:25	Fine	20369	2.8962	2.9083	9920.87	9921.87	1.00	1.19	1.19	1.19	71	170.0
11-May-17	9:05	Fine	20384	2.8443	2.8551	9945.87	9946.87	1.00	1.07	1.07	1.07	64	168.0
11-May-17	10:30	Fine	20385	2.8518	2.8604	9946.87	9947.87	1.00	1.18	1.18	1.18	71	121.2
11-May-17	13:00	Fine	20424	2.5001	2.5073	9947.87	9948.87	1.00	1.18	1.18	1.18	71	101.4
17-May-17	9:30	Fine	20395	2.8546	2.8634	9972.87	9973.87	1.00	1.18	1.18	1.18	71	123.9
17-May-17	11:00	Fine	20409	2.8425	2.8476	9973.87	9974.87	1.00	1.18	1.18	1.18	71	71.8
17-May-17	13:00	Fine	20406	2.8662	2.8758	9974.87	9975.87	1.00	1.18	1.18	1.18	71	135.1
23-May-17	9:25	Cloudy	20620	2.5496	2.5545	9999.87	10000.87	1.00	1.18	1.18	1.18	71	69.0
23-May-17	11:00	Cloudy	20614	2.5822	2.5861	10000.87	10001.87	1.00	1.18	1.18	1.18	71	54.9
23-May-17	13:00	Cloudy	20603	2.5252	2.5322	10001.87	10002.87	1.00	1.18	1.18	1.18	71	98.6



Location: CMA2a - Causeway Bay Community Centre

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 169.5

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
28-Apr-17	8:00	Fine	19989	2.8681	2.9012	19477.15	19501.15	24.00	0.97	0.97	0.97	1397	23.7
4-May-17	8:00	Rainy	20283	2.5741	2.6533	19504.15	19528.15	24.00	1.04	1.04	1.04	1491	53.1
10-May-17	8:00	Fine	20365	2.9174	3.0895	19531.15	19555.15	24.00	1.03	1.03	1.03	1486	115.8
16-May-17	8:00	Cloudy	19711	2.8331	2.8950	19558.16	19582.16	24.00	0.96	0.96	0.96	1382	44.8
22-May-17	8:00	Cloudy	20402	2.8425	2.9315	19585.16	19609.16	24.00	0.96	0.96	0.96	1381	64.4

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 323.4

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Apr-17	8:30	Fine	20175	2.5861	2.5904	19501.15	19502.15	1.00	0.97	0.97	0.97	58	74.0
29-Apr-17	10:10	Fine	20168	2.5179	2.5212	19502.15	19503.15	1.00	0.97	0.97	0.97	58	56.8
29-Apr-17	13:00	Fine	20289	2.5573	2.5628	19503.15	19504.15	1.00	0.97	0.97	0.97	58	94.6
5-May-17	9:45	Fine	20327	2.9134	2.9179	19528.15	19529.15	1.00	0.96	0.96	0.96	58	77.9
5-May-17	13:00	Fine	20331	2.8938	2.9010	19529.15	19530.15	1.00	0.96	0.96	0.96	58	124.7
5-May-17	15:21	Fine	20333	2.8930	2.9038	19530.15	19531.15	1.00	0.96	0.96	0.96	58	187.0
11-May-17	9:10	Fine	20361	2.9211	2.9260	19555.15	19556.15	1.00	0.96	0.96	0.96	57	85.2
11-May-17	10:30	Fine	20431	2.4988	2.5036	19556.15	19557.15	1.00	1.10	1.10	1.10	66	72.5
11-May-17	13:00	Fine	20425	2.5083	2.5140	19557.15	19558.15	1.00	1.03	1.03	1.03	62	92.2
17-May-17	9:35	Fine	20394	2.8437	2.8484	19582.16	19583.16	1.00	0.96	0.96	0.96	58	81.6
17-May-17	11:00	Fine	20396	2.8482	2.8498	19583.16	19584.16	1.00	0.96	0.96	0.96	58	27.8
17-May-17	13:00	Fine	20405	2.8426	2.8468	19584.16	19585.16	1.00	0.96	0.96	0.96	58	72.9
23-May-17	9:25	Cloudy	20621	2.6321	2.6344	19609.16	19610.16	1.00	1.10	1.10	1.10	66	34.7
23-May-17	11:00	Cloudy	20615	2.5761	2.5779	19610.16	19611.16	1.00	1.10	1.10	1.10	66	27.2
23-May-17	13:00	Cloudy	20604	2.5405	2.5427	19611.16	19612.16	1.00	0.96	0.96	0.96	57	38.3



Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 171

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
28-Apr-17	8:00	Fine	19987	2.8477	2.9375	6967.72	6991.72	24.00	1.16	1.16	1.16	1666	53.9
4-May-17	8:00	Rainy	20248	2.5766	2.6827	6994.72	7018.72	24.00	1.15	1.15	1.15	1655	64.1
10-May-17	8:00	Fine	20334	2.9015	3.0965	7021.73	7045.73	24.00	1.15	1.14	1.15	1650	118.2
16-May-17	8:00	Cloudy	20387	2.8635	2.9145	7049.74	7073.74	24.00	1.15	1.15	1.15	1651	30.9
22-May-17	8:00	Cloudy	20401	2.8539	2.9298	7076.74	7100.74	24.00	1.15	1.14	1.15	1650	46.0

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 311.3

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Apr-17	8:30	Fine	20176	2.5786	2.5864	6991.72	6992.72	1.00	1.16	1.16	1.16	69	112.5
29-Apr-17	9:50	Fine	20169	2.5736	2.5809	6992.72	6993.72	1.00	1.16	1.16	1.16	69	105.3
29-Apr-17	10:52	Fine	20290	2.5718	2.5790	6993.72	6994.72	1.00	1.16	1.16	1.16	69	103.8
5-May-17	9:20	Fine	20254	2.5598	2.5693	7018.73	7019.73	1.00	1.15	1.15	1.15	69	137.8
5-May-17	10:50	Fine	20252	2.5842	2.5964	7019.73	7020.73	1.00	1.15	1.15	1.15	69	177.0
5-May-17	14:50	Fine	20371	2.9154	2.9316	7020.73	7021.73	1.00	1.15	1.15	1.15	69	235.0
11-May-17	8:50	Fine	20421	2.4998	2.5038	7045.74	7046.74	1.00	1.14	1.14	1.14	69	58.2
11-May-17	13:00	Fine	20426	2.5076	2.5131	7046.74	7047.74	1.00	1.14	1.14	1.14	69	80.1
11-May-17	17:00	Fine	20383	2.8463	2.8518	7047.74	7048.74	1.00	1.14	1.14	1.14	69	80.1
17-May-17	9:15	Fine	20392	2.8505	2.8535	7073.74	7074.74	1.00	1.01	1.01	1.01	61	49.4
17-May-17	10:35	Fine	20410	2.8295	2.8339	7074.74	7075.74	1.00	1.15	1.15	1.15	69	64.0
17-May-17	13:00	Fine	20399	2.8384	2.8419	7075.74	7076.74	1.00	1.15	1.15	1.15	69	50.9
23-May-17	9:02	Cloudy	20624	2.6311	2.6334	7100.74	7101.74	1.00	1.14	1.14	1.14	69	33.5
23-May-17	10:50	Cloudy	20617	2.5264	2.5293	7101.74	7102.74	1.00	1.14	1.14	1.14	69	42.2
23-May-17	13:00	Cloudy	20606	2.5990	2.6025	7102.74	7103.74	1.00	1.14	1.14	1.14	69	51.0



Location: CMA4a - SPCA

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 171.2

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Apr-17	13:00	Fine	20284	2.5574	2.6429	23768.27	23792.27	24.00	0.92	0.92	0.92	1330	64.3
4-May-17	8:00	Rainy	20259	2.5827	2.6645	23792.27	23816.27	24.00	0.92	0.92	0.92	1323	61.8
10-May-17	8:00	Fine	20367	2.9088	3.0387	23819.29	23843.29	24.00	0.92	0.91	0.92	1318	98.6
16-May-17	8:00	Cloudy	20432	2.5155	2.5525	23846.29	23870.29	24.00	0.85	0.85	0.85	1224	30.2
22-May-17	8:00	Cloudy	20400	2.8468	2.9035	23873.29	23897.29	24.00	0.78	0.78	0.78	1127	50.3

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 28 April 2017 to 29 April 2017.

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 312.5

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Apr-17	8:30	Fine	20247	2.5861	2.5938	23765.27	23766.27	1.00	0.92	0.92	0.92	55	138.8
29-Apr-17	9:55	Fine	20170	2.5724	2.5777	23766.27	23767.27	1.00	0.92	0.92	0.92	55	95.5
29-Apr-17	11:00	Fine	20293	2.5688	2.5737	23767.27	23768.27	1.00	0.92	0.92	0.92	55	88.3
5-May-17	9:25	Fine	20326	2.9080	2.9144	23816.28	23817.28	1.00	0.79	0.79	0.79	47	135.8
5-May-17	13:00	Fine	20330	2.9119	2.9192	23817.28	23818.28	1.00	0.79	0.79	0.79	47	154.9
5-May-17	14:30	Fine	20249	2.5733	2.5810	23818.28	23819.28	1.00	0.79	0.79	0.79	47	163.4
11-May-17	8:50	Fine	20362	2.9258	2.9332	23843.29	23844.29	1.00	0.91	0.91	0.91	55	134.9
11-May-17	10:15	Fine	20356	2.9070	2.9150	23844.29	23845.29	1.00	0.91	0.91	0.91	55	145.9
11-May-17	13:00	Fine	20427	2.5323	2.5364	23845.29	23846.29	1.00	0.91	0.91	0.91	55	74.8
17-May-17	9:15	Fine	20393	2.8553	2.8589	23870.29	23871.29	1.00	0.92	0.92	0.92	55	65.5
17-May-17	10:30	Fine	20412	2.8200	2.8225	23871.29	23872.29	1.00	0.92	0.92	0.92	55	45.5
17-May-17	13:00	Fine	20407	2.8600	2.8630	23872.29	23873.29	1.00	0.92	0.92	0.92	55	54.6
23-May-17	9:00	Cloudy	20623	2.6474	2.6484	23897.30	23898.30	1.00	0.78	0.78	0.78	47	21.3
23-May-17	10:50	Cloudy	20618	2.5606	2.5622	23898.30	23899.30	1.00	0.78	0.78	0.78	47	34.1
23-May-17	13:00	Cloudy	20607	2.5765	2.5783	23899.30	23900.30	1.00	0.78	0.78	0.78	47	38.4



Location: CMA5b - Pedestrian Plaza

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 181

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
28-Apr-17	8:00	Fine	19990	2.8503	2.9953	8322.75	8346.75	24.00	0.77	0.76	0.77	1102	131.6
4-May-17	8:00	Rainy	20287	2.5761	2.6398	8349.75	8373.75	24.00	0.76	0.76	0.76	1093	58.3
10-May-17	8:00	Fine	20370	2.8924	3.1178	8376.75	8400.75	24.00	0.88	0.88	0.88	1267	177.9
17-May-17	16:20	Fine	20550	2.5669	2.7077	8406.76	8430.76	24.00	0.82	0.82	0.82	1179	119.4
22-May-17	8:00	Cloudy	20536	2.5506	2.6304	8430.79	8454.79	24.00	0.79	0.79	0.79	1133	70.4

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 16 May 2017 to 17 May 2017.

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 332

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Apr-17	8:30	Fine	20178	2.5946	2.6054	8346.75	8347.75	1.00	0.76	0.76	0.76	46	235.6
29-Apr-17	9:33	Fine	20173	2.5757	2.5886	8347.75	8348.75	1.00	0.76	0.76	0.76	46	281.4
29-Apr-17	10:40	Fine	20294	2.5919	2.6010	8348.75	8349.75	1.00	0.89	0.89	0.89	53	170.6
5-May-17	8:05	Fine	20262	2.5573	2.5696	8373.75	8374.75	1.00	0.76	0.76	0.76	46	270.2
5-May-17	10:04	Fine	20329	2.8965	2.9095	8374.75	8375.75	1.00	0.76	0.76	0.76	46	285.6
5-May-17	13:00	Fine	20374	2.8945	2.9125	8375.75	8376.75	1.00	0.91	0.91	0.91	55	328.2
11-May-17	8:30	Fine	20263	2.5582	2.5647	8400.76	8401.76	1.00	0.82	0.82	0.82	49	132.6
11-May-17	9:45	Fine	20360	2.8952	2.9005	8401.76	8402.76	1.00	0.75	0.75	0.75	45	117.0
11-May-17	13:00	Fine	20430	2.4996	2.5082	8402.76	8403.76	1.00	0.88	0.88	0.88	53	163.1
17-May-17	8:30	Fine	20537	2.5667	2.5757	8403.76	8404.76	1.00	0.76	0.76	0.76	45	198.3
17-May-17	13:00	Fine	20408	2.8443	2.8535	8404.76	8405.76	1.00	0.76	0.76	0.76	45	202.8
17-May-17	14:28	Fine	20551	2.5723	2.5860	8405.76	8406.76	1.00	0.76	0.76	0.76	45	301.9
23-May-17	8:25	Cloudy	20578	2.5833	2.5855	8454.80	8455.80	1.00	0.76	0.76	0.76	45	48.6
23-May-17	10:00	Cloudy	20619	2.5447	2.5482	8455.80	8456.80	1.00	0.82	0.82	0.82	49	71.4
23-May-17	13:00	Cloudy	20584	2.5931	2.6002	8456.80	8457.80	1.00	0.79	0.82	0.80	48	147.6



Location: MA1e - International Finance Centre (Eastern Wing)

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 173.4

Limit Level ($\mu\text{g}/\text{m}^3$) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
28-Apr-17	8:00	Fine	20064	2.4950	2.6108	20659.53	20683.53	24.00	1.02	1.02	1.02	1467	78.9
5-May-17	16:36	Fine	20276	2.5883	2.8092	20703.94	20727.94	24.00	1.09	1.09	1.09	1575	140.3
10-May-17	8:00	Fine	20363	2.8965	3.0237	20727.94	20751.94	24.00	1.01	1.01	1.01	1459	87.2
16-May-17	8:00	Cloudy	20338	2.9048	2.9244	20754.94	20778.94	24.00	1.01	1.01	1.01	1459	13.4
22-May-17	8:00	Cloudy	20352	2.9143	2.9834	20781.94	20805.94	24.00	1.05	1.09	1.07	1545	44.7

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 4 May 2017 to 5 May 2017.

Report on 1-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 325.1

Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Apr-17	8:43	Fine	20182	2.5371	2.5436	20683.53	20684.53	1.00	1.06	1.06	1.06	64	102.4
29-Apr-17	9:45	Fine	20181	2.5679	2.5751	20684.53	20685.53	1.00	1.10	1.10	1.10	66	109.2
29-Apr-17	10:48	Fine	20165	2.5546	2.5614	20685.53	20686.53	1.00	1.10	1.10	1.10	66	103.2
5-May-17	10:00	Fine	20279	2.5994	2.6085	20700.94	20701.94	1.00	1.01	1.01	1.01	61	149.5
5-May-17	13:00	Fine	20277	2.6098	2.6171	20701.94	20702.94	1.00	1.09	1.09	1.09	66	111.2
5-May-17	14:20	Fine	20278	2.6062	2.6150	20702.94	20703.94	1.00	1.01	1.01	1.01	61	144.5
11-May-17	9:35	Fine	20337	2.9086	2.9131	20751.94	20752.94	1.00	1.05	1.05	1.05	63	71.3
11-May-17	10:41	Fine	20336	2.8992	2.9045	20752.94	20753.94	1.00	1.05	1.05	1.05	63	84.0
11-May-17	13:00	Fine	20339	2.9017	2.9058	20753.94	20754.94	1.00	1.05	1.05	1.05	63	64.9
17-May-17	9:45	Fine	20355	2.9045	2.9073	20778.94	20779.94	1.00	1.09	1.09	1.09	66	42.7
17-May-17	10:48	Fine	20354	2.9337	2.9407	20779.94	20780.94	1.00	1.09	1.09	1.09	66	106.8
17-May-17	13:00	Fine	20353	2.9239	2.9304	20780.94	20781.94	1.00	1.09	1.09	1.09	66	99.1
23-May-17	8:02	Cloudy	20611	2.5397	2.5412	20805.94	20806.94	1.00	1.05	1.05	1.05	63	23.8
23-May-17	10:30	Cloudy	20582	2.5621	2.5634	20806.94	20807.94	1.00	1.09	1.09	1.09	66	19.8
23-May-17	13:00	Cloudy	20609	2.5551	2.5573	20807.94	20808.94	1.00	1.09	1.09	1.09	66	33.6



Location: MA1w - International Finance Centre (Western Wing)

Report on 24-hour TSP monitoring

Action Level ($\mu\text{g}/\text{m}^3$) - 173.4
Limit Level ($\mu\text{g}/\text{m}^3$) - 260




Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
28-Apr-17	8:00	Fine	20060	2.4945	2.5306	20440.85	20464.85	24.00	1.32	1.32	1.32	1896	19.0
4-May-17	8:00	Rainy	20055	2.5006	2.6275	20467.85	20491.85	24.00	1.31	1.31	1.31	1888	67.2
10-May-17	8:00	Fine	20272	2.5983	2.7576	20494.86	20518.86	24.00	1.31	1.31	1.31	1884	84.6
16-May-17	8:00	Cloudy	20340	2.9015	2.9638	20521.86	20545.86	24.00	1.31	1.31	1.31	1885	33.1
22-May-17	8:00	Cloudy	20348	2.9523	2.9806	20548.87	20572.87	24.00	1.31	1.31	1.31	1884	15.0

Report on 1-hour TSP monitoring




Action Level ($\mu\text{g}/\text{m}^3$) - 325.1
Limit Level ($\mu\text{g}/\text{m}^3$) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, m^3/min			Total Volume, m^3	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, Q_{si}	Final, Q_{sf}	Average		
29-Apr-17	8:46	Fine	20163	2.5560	2.5661	20464.85	20465.85	1.00	1.32	1.32	1.32	79	128.0
29-Apr-17	9:49	Fine	20184	2.5791	2.5868	20465.85	20466.85	1.00	1.32	1.32	1.32	79	97.6
29-Apr-17	10:51	Fine	20183	2.5925	2.5987	20466.85	20467.85	1.00	1.32	1.32	1.32	79	78.6
5-May-17	8:45	Fine	20275	2.5923	2.6007	20491.85	20492.85	1.00	1.31	1.31	1.31	79	106.8
5-May-17	10:31	Fine	20274	2.5916	2.6000	20492.85	20493.85	1.00	1.31	1.31	1.31	79	106.8
5-May-17	13:00	Fine	20273	2.6030	2.6094	20493.85	20494.85	1.00	1.31	1.31	1.31	79	81.4
11-May-17	9:47	Fine	20343	2.9319	2.9362	20518.86	20519.86	1.00	1.31	1.31	1.31	78	54.8
11-May-17	10:49	Fine	20342	2.8977	2.9053	20519.86	20520.86	1.00	1.42	1.42	1.42	85	89.3
11-May-17	13:00	Fine	20341	2.8991	2.9056	20520.86	20521.86	1.00	1.42	1.42	1.42	85	76.4
17-May-17	9:48	Fine	20351	2.9206	2.9269	20545.86	20546.86	1.00	1.31	1.31	1.31	79	80.3
17-May-17	10:50	Fine	20350	2.9301	2.9362	20546.86	20547.86	1.00	1.31	1.31	1.31	79	77.7
17-May-17	13:00	Fine	20349	2.9294	2.9354	20547.86	20548.86	1.00	1.31	1.31	1.31	79	76.4
23-May-17	8:05	Cloudy	20610	2.5487	2.5502	20572.87	20573.87	1.00	1.31	1.31	1.31	78	19.1
23-May-17	10:35	Cloudy	20581	2.5661	2.5688	20573.87	20574.87	1.00	1.31	1.31	1.31	78	34.4
23-May-17	13:00	Cloudy	20608	2.5598	2.5627	20574.87	20575.87	1.00	1.31	1.31	1.31	78	37.0

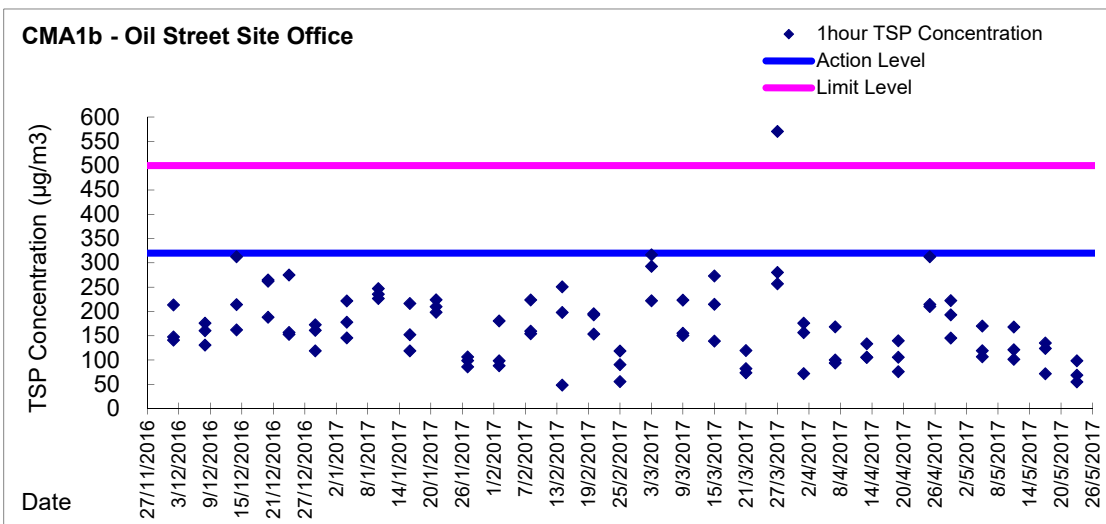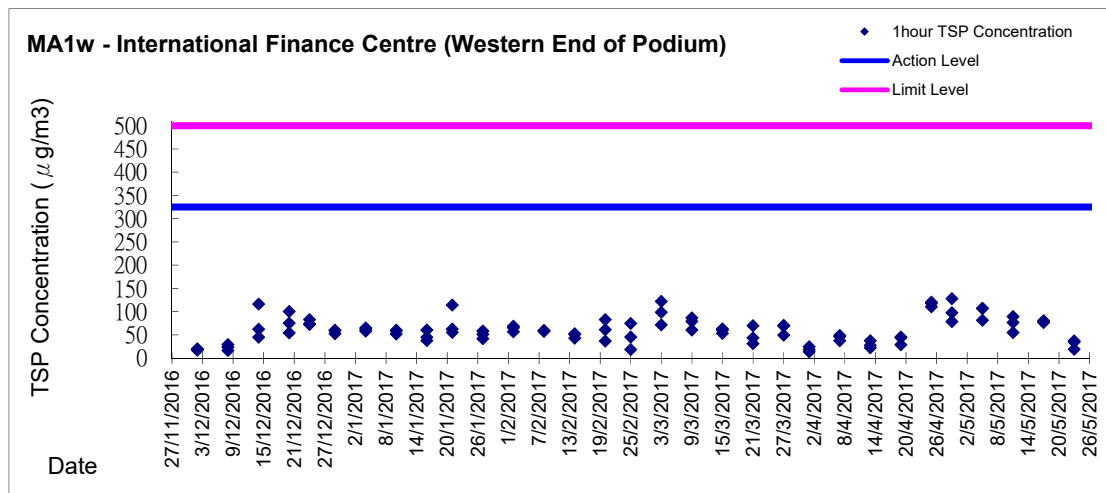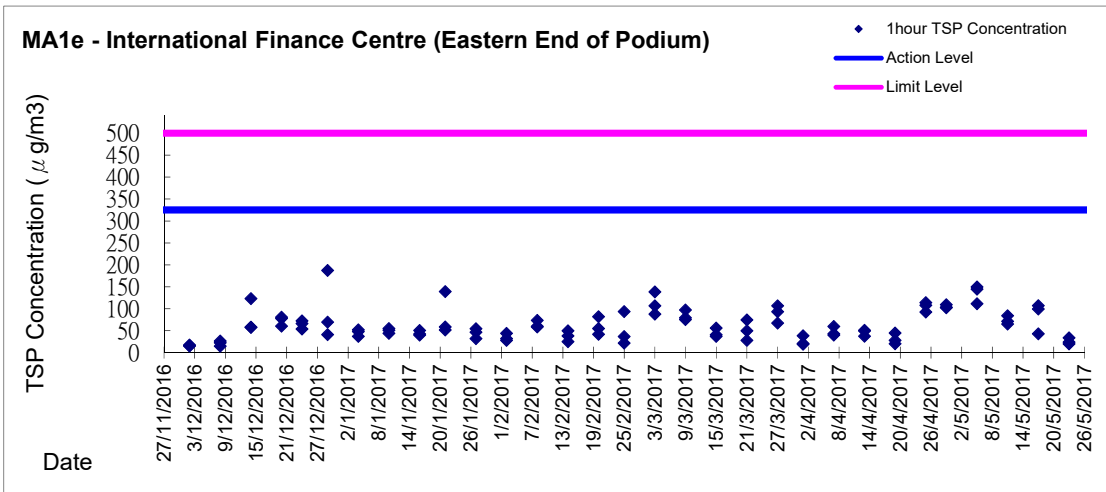
Graphic Presentation of 1 hour TSP Result



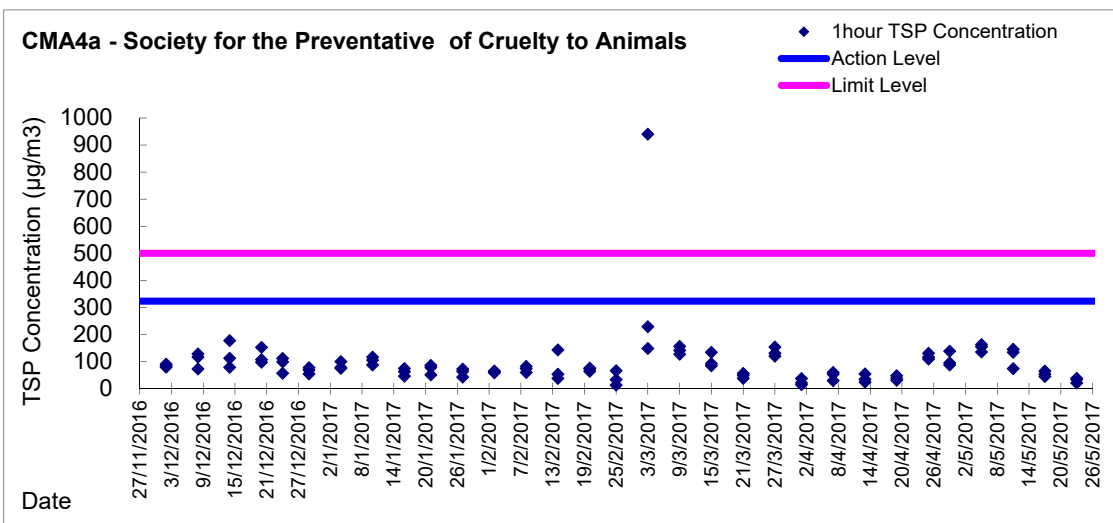
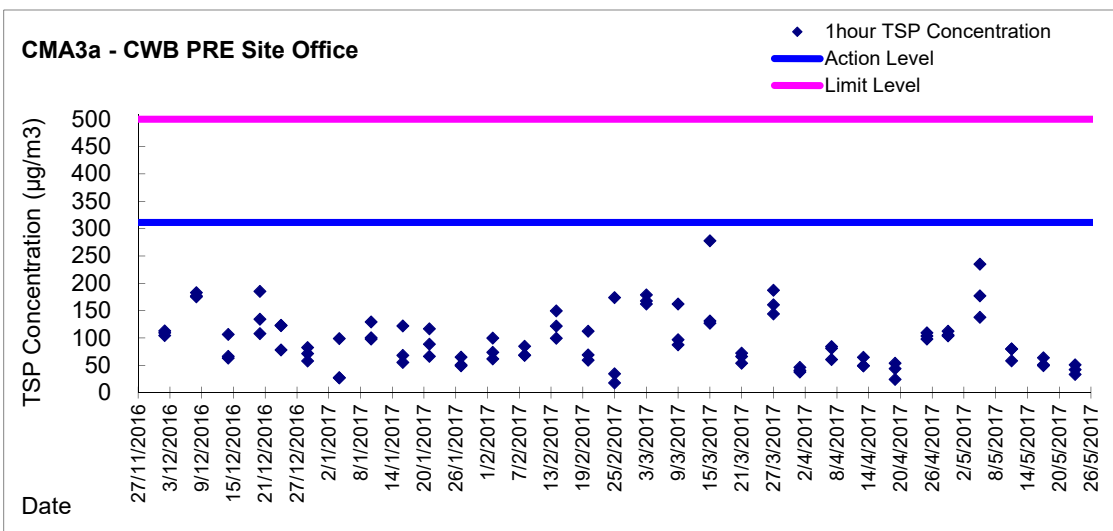
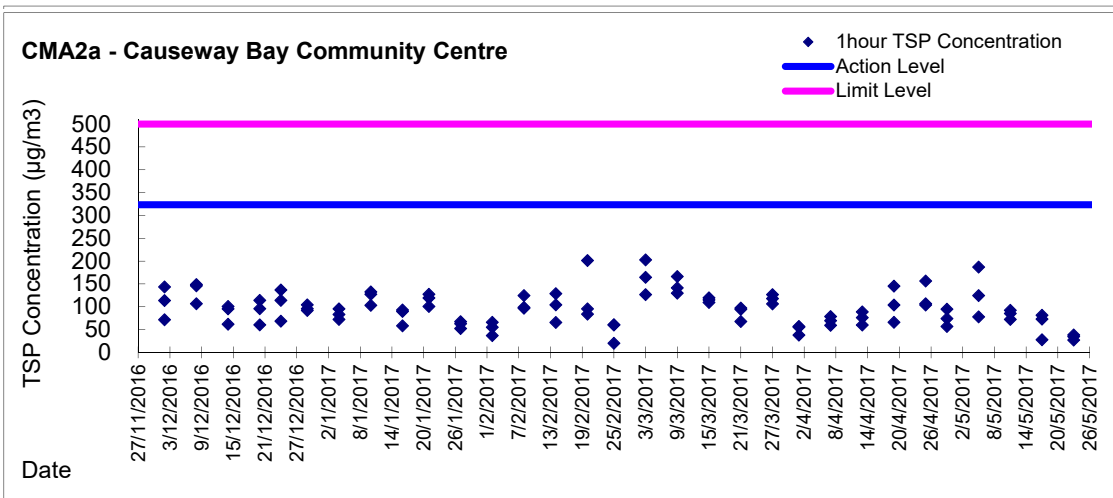
Graphic Presentation of 1 hour TSP Result





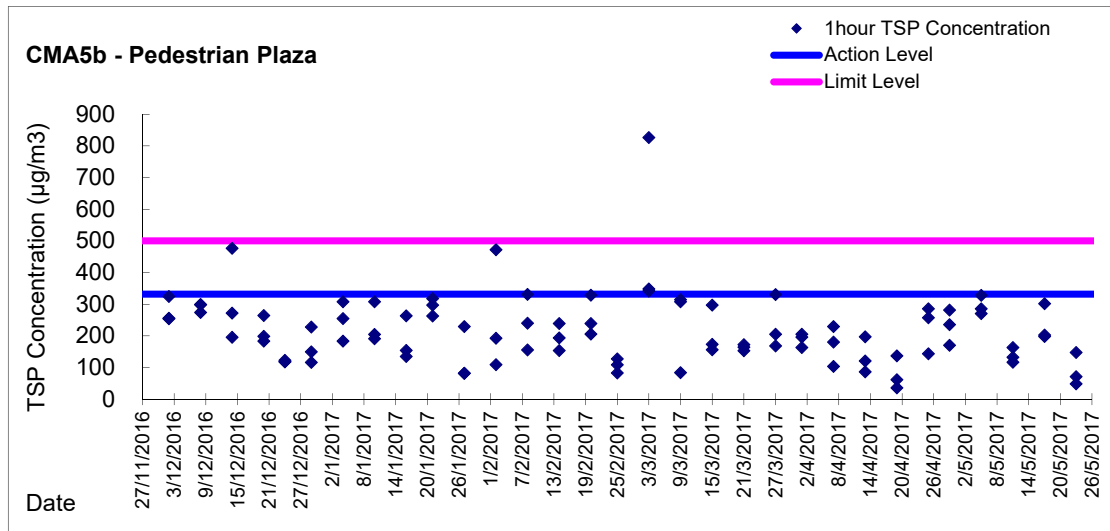
Graphic Presentation of 1 hour TSP Result



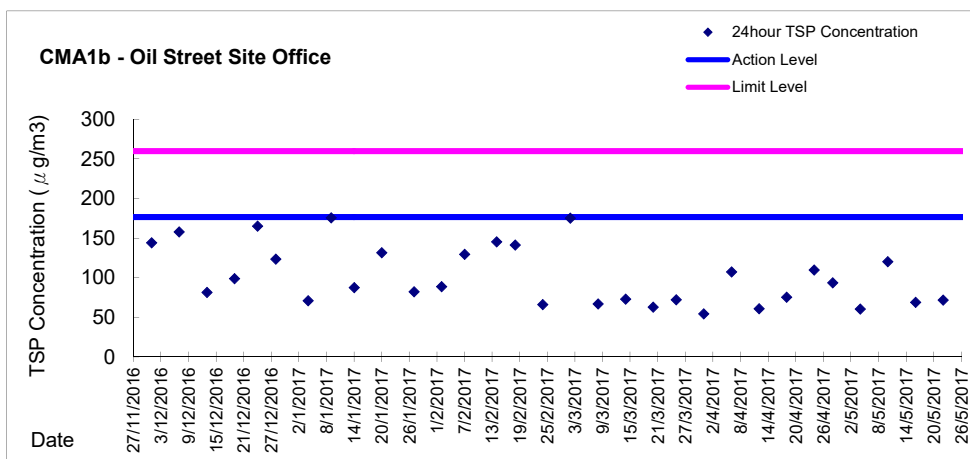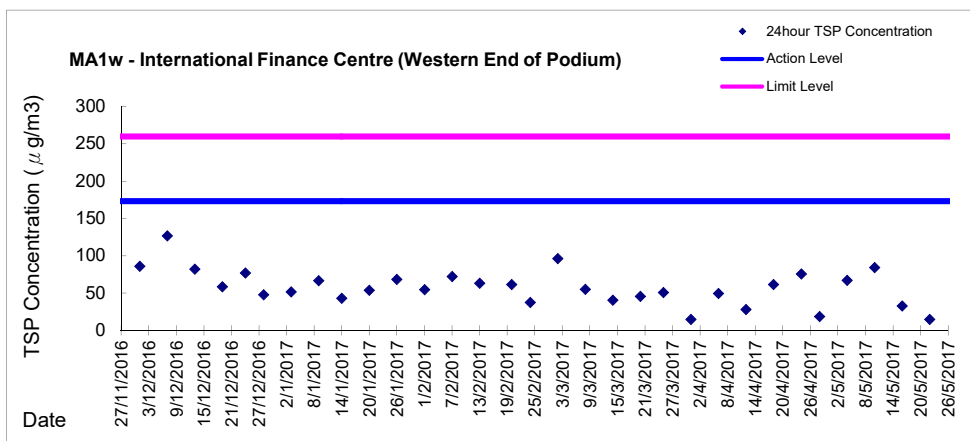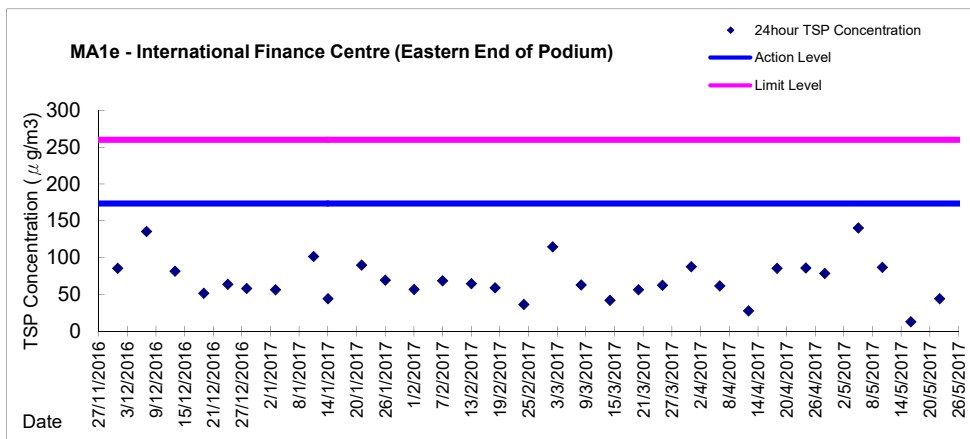
Graphic Presentation of 24 hour TSP Result



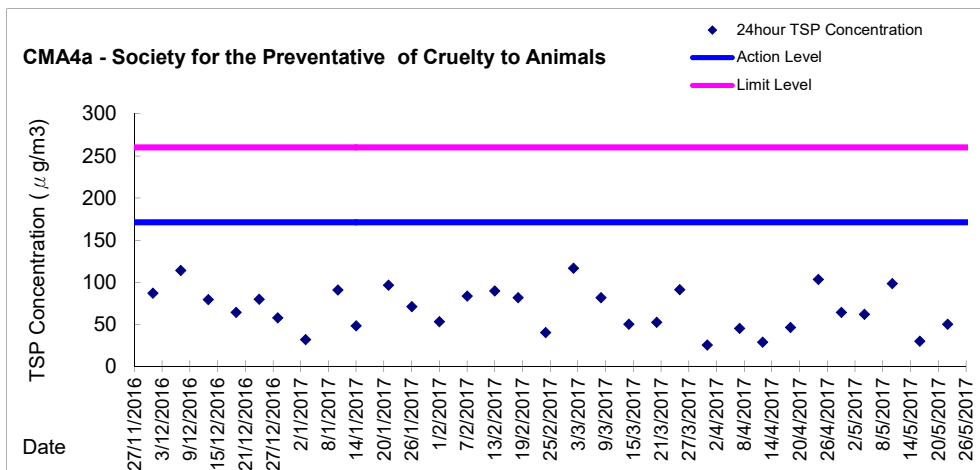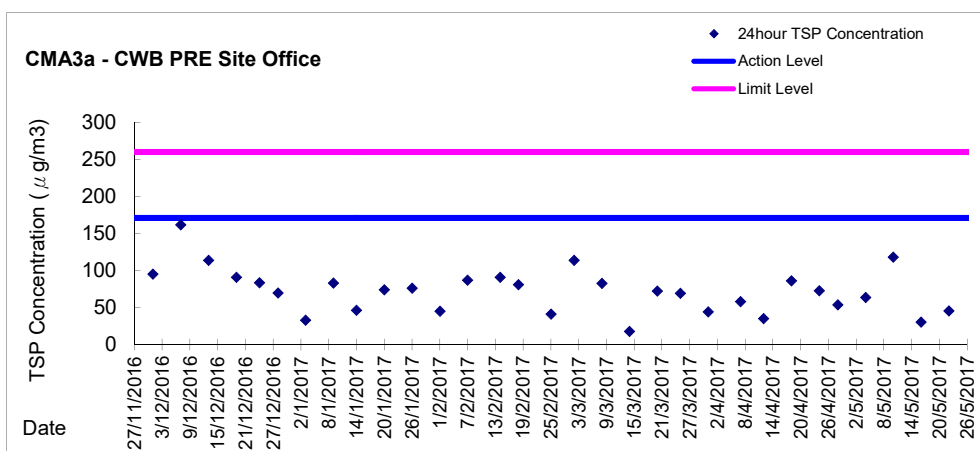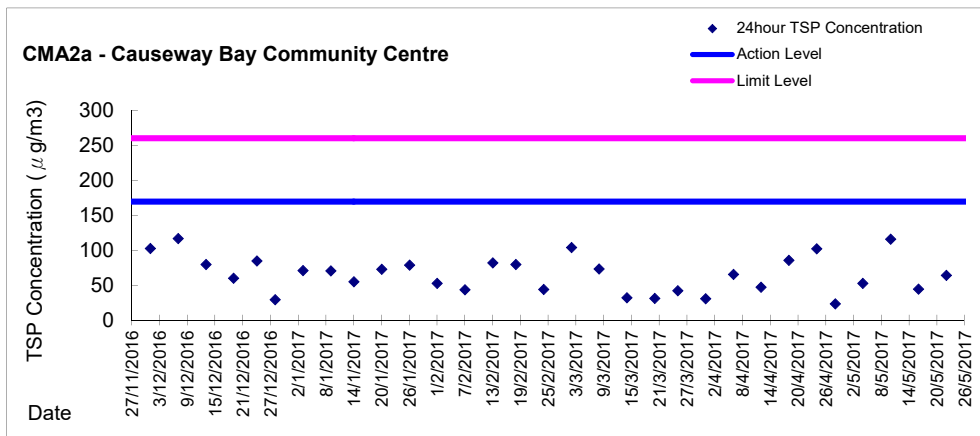Graphic Presentation of 24 hour TSP Result



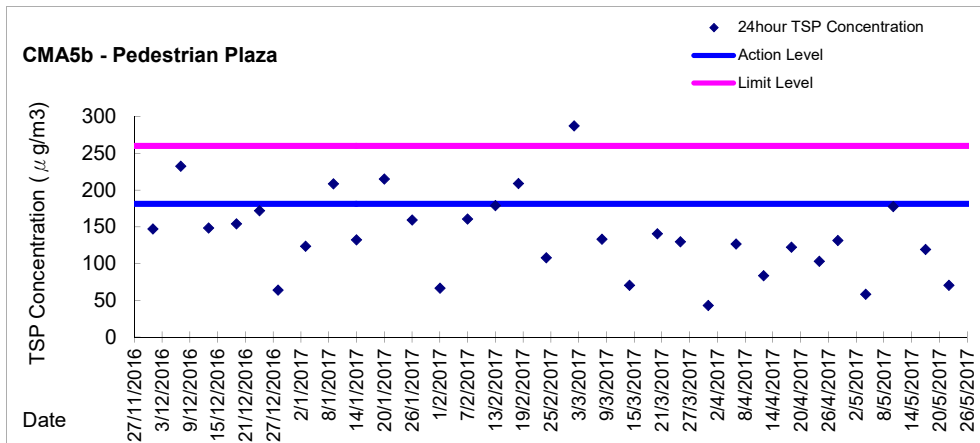Graphic Presentation of 24 hour TSP Result





Appendix 5.1

Event Action Plans



Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	1. Notify ER, IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC, ER and Contractor; 4. Discuss with the IEC and Contractor on remedial measures required; 5. Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Review the investigation results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Advise the ER on the effectiveness of the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Submit noise mitigation proposals to IEC and ER; 2. Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified)



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit Level being exceeded	1. Inform IEC, ER, Contractor and EPD; 2. Repeat measurements to confirm findings; 3. Increase monitoring frequency; 4. Identify source and investigate the cause of exceedance; 5. Carry out analysis of Contractor's working procedures; 6. Discuss with the IEC, Contractor and ER on remedial measures required; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Supervise the implementation of remedial measures; 5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Submit further proposal if problem still not under control; 5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)

**Event / Action Plan for Construction Air Quality**

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
LIMIT LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)



Appendix 6.1

Complaint Log



Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
110723a	23/07/2011	Ms. Law at Victoria Centre by ICC no. 1-303887687	North Point	She concerned that Highways Department published a notice in their Management Office about construction works will be conducted from 0700 hours to 2300 hours during July to December 2011 including Saturday, Sunday and public holiday.	1) It was referred by AECOM to ET on 28 July 2011 2) RSS confirmed that the notice was prepared by Victoria Centre 'a Management office to their resident and the advice was only given on the extension construction works (for Contract HY/2009/15) to 7am-9pm Monday to Saturday except Public Holidays and Sundays. 3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid-August 2011. 4) No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 19 and 25 July 2011 during daytime and evening time period while breaking and excavation works were observed during monitoring. 5) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	Closed
110723b	23/07/2011	Ms. Yau at Block 2, Victoria Centre by ICC no. 1-304013959	North Point	Reclamation work was conducted at Causeway Bay Typhoon Shelter at 7am on 23 July 2011. She complained that the works shall be started later to minimize the noise nuisance to the vicinity of the residents in early morning	1) It was referred by AECOM to ET on 8 August 2011 2) RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents. 3) With reference to the construction noise monitoring at Victoria Centre, no exceedance was recorded on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring 4) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	Closed
110727a	27/07/2011	Mr. Law from Victoria Centre Management Office by ICC no. 1-304616162	North Point	It was complained by Mr. Law from Victoria Centre Management Office on 27 July 2011 regarding construction noise generated by the construction operations of	1) It was referred by AECOM to ET on 28 July 2011 2) RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents. 3) No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 25 July and	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Central-Wanchai Bypass at noon rather than in morning at 7am.	4 August 2011 during daytime and evening time period while breaking and excavation works were observed during monitoring. 5) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. No further complaint from complainant was received after proposed the mitigation measure.	
110727b	27/07/2011	Ms. Chiu by ICC no.1-304615409	North Point	Noise nuisance from the excavation works for the Highways Department adjacent to the Victoria Centre was conducted from 7am	1) It was referred by AECOM to ET on 28 July 2011 2) With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 25 July and 4 and 10 August 2011 during daytime while breaking and excavation works were undertaken during monitoring. 3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am.	Closed
	07/08/2011				4) However, complainant did not satisfy with the response on the noise nuisance from the rock-breaking during morning in front of Victoria Centre and then further complaint via 1823 on 7 August 2011. 5) Highways contacted the complainant on 15 August 2011 that the noisy rock breaking operation had been completed. <i>Remarks: There will be counted as two complaints in this complaint log.</i>	
110730	30/07/2011	Mr. Tsui by ICC no. 1-305074350	Central	Construction noise generated by operations of Central-Interchange which is near the spa room at Four-Season Hotel. Also, the complaint enquired the commencement time of the construction on Saturday.	1) It was referred by AECOM to ET on 1 August 2011. 2) RSS confirmed that noisy plants from 2 vibratory hammers have been conducted in alternating manner for piling and drilling works for diaphragm wall construction. 3) With reference to the construction noise monitoring at IFC Western End of Podium, no exceedance was recorded on 4 August 2011 during monitoring while sheet piling works were undertaken during monitoring. 4) In order to reduce the noise impact to nearby noise sensitive receivers, Contractor has been implemented the following noise mitigation measures: - Erection of acoustic lining at the hoarding next to Four Seasons Hotel; - Temporary noise barrier with extended acoustic lining; - Reduced in plant such that only have one vibration hammer operating at the west side near Four	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Seasons Hotel instead of 2 5) In conclusion, it was related to the construction works under Contract HY/2009/18 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	
110810	10/08/2011	Mr. Yip by ICC no. 1 – 306740207	North Point	Muddy water was discharged from work site to the seafront near Oil Street during heavy rain. The environmental protection measures were not good enough and are needed to rectify.	1) It was referred by AECOM to ET on 17 August 2011. 2) Confirmed with RE, Muddy water was caused by a heap of earth being washed to the sea by heavy rain. The heap of earth was referred as a small stockpile placed close to the seafront in front of Oil Street within the site area under handover transition period from contract HY/2009/11 to contract HY/2009/19. The necessary mitigation measures to protect the small stockpile against rainfall were missing at the time of complaint. 3) Due to the missing of mitigation measures to protect the small stockpile during handover transition period, loose material was washed into the harbour when heavy rain came. Muddy water was formed and dispersed in the sea that caused the water quality and visual concern to the public. The complaint was considered as valid. 4) Contractors were advised to relocate the loose materials away from the coastline as far as practicable. Any loose material placed which needed to be placed near the coastline shall be properly compacted or covered as appropriate. To avoid any further environmental deficiency, Contractors shall ensure all necessary environmental mitigation measures will not be missing during site area handover.	Closed
110817	17/08/2011	ICC no. 1-307657681	North Point	Visual impact generated by light from a large amount of spot-lights on the barge during mid-night nearby City Garden.	1) It was referred by AECOM to ET on 23 August 2011 2) RSS confirmed that some non-essential lights were turned on during night-time period which caused the nuisance to the nearby residents. In addition, absence of lighting shields at flood lights results in visual glare to the complaint at night-time. 3) Follow-up action had been taken by contractor that switches off all non-essential lights to minimized nuisance to the nearby residents. The complainant satisfied to the practice and no further complaint was received after that.	Closed
110826	26/08/2011	Grand Hyatt and a complainant by ICC	Wan Chai	Construction noise and vibration nuisance generated from the works at Convention Avenue and inside the HKCEC1	1) Confirmed with the Resident Site Staff that the construction works were referred to the Contractor HK/2009/01. 2) The Excavator mounted breaker at Convention Avenue	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				reclamation area.	and Drilling rig at HKCEC1 reclamation area were the dominant construction noise source during this period. 3) The drilling rig at HKCEC1 reclamation area and excavator mounted breaker at Convention Avenue were then temporary suspended after received the complaint. 4) Investigation revealed that the erected noise barrier (4m cantilevered movable noise barrier for the drilling rig and 1m movable noise barrier for the excavator mounted breaker) were not located close to the plants to provide adequate noise screening. 5) Contractor was advised to avoid concurrent operation of construction plants at site. Further enhancement of movable noise barriers at HKCEC1 and providing noise enclosure for the excavator mounted breaker at Convention Avenue are needed. 6) Further site investigation and checking on 31 August and 7 September 2011 revealed that the implemented noise mitigation measures were in proper and minimize the noise impact.	
110826A	26/08/2011	A complaint letter from Mr. Au of Cayley Property of City Garden	North Point	Harbor front adjacent to their water intake suction which caused 3 times of system breakdown of the sea water pump on 9, 22 and 25 August 2011.	1) It was referred by AECOM to ET on 29 August 2011 2) Confirmed with the Resident Site Staff that the construction works were referred to the Contractors HY/2009/11 and HY/2009/19. 3) The pump is located on the site area of HY/2009/19 4) A temporary garbage defender was installed on 23 July 2011 by HY/2009/11 and the shape of the defender was adjusted on 8 August 2011 in order to exclude the outfall. 5) An ad hoc inspection of the effectiveness of garbage defender was conducted with RSS (CWB project team), contractor of HY/2009/11 and HY/2009/19 and IECon 29 August 2011. Inspection report of it was submitted to RSS on 19 September 2011. 5) Daily cleaning near the water intake was conducted twice a day by contractor HY/2009/19. 6) In response to City Garden request, the contractors have set up the temporary garbage defender in function and collect the floating refuses, but cannot eliminate all refuses, in particular the refuse come from sea bed from entering the intake. 6) According to the complaint letter from Cayley Property, the outcomes of the preventive measures were not complying with their expectation. 7) During on-site inspection, floating refuses observed	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					occasionally outside the garbage defender. No conclusion could be made for the source of these floating refuses. On the other hand, some of the floating refuses were observed immigrating in the protective zone during investigation 8) All daily cleaning actions had been taken by contractor to minimize floating refuse inside the construction site. It was noted that the intake (land side) is open access to public, so that many activities such as fishing, feeding fish were conducted there even though a notice has already hoisted. Also, tripping of rubbish by the passers-by could result in a lot of rubbish accumulated around the intake point. 9) Referring to the record provided by CPML, there were a lot of nylon/ plastic bags and nylon wire mesh that matched those rubbishes generated from the public activities. 10) Contractors have fulfilled the requirement of site cleanness and no exceedance was recorded during Water Quality Monitoring. It is consider the cause of this complaint is not related to project and environmental issue in this project as well. No more complaint received after ad-hoc inspection	
111014	14/10/2011	The complainant, Ms. Tam complained via hotline 1823	Wan Chai	The polluted fumes and exhaust from the excavation by sub-contractor of CEDD on pedestrian way outside no.25 Harbour Road (in front of the Harbour Centre)	1) RSS notified ET to carry out investigation on 17 October 2011. 2) ET confirmed with the Resident Site Staff that the location of the excavator was within site area of Contract no. HK/2009/02 undertaking the water cooling main reprovision works along the Harbour Road. The plants including the excavator have been checked before using at the site. However, the polluted fumes and exhausted from the excavator was caused due to insufficient maintenance of the plant after using at site. 3) After receiving the complaint, the excavator was then removal off-site for checking and maintenance works on 17 October 2011. 4) Contractor was reminded to enhance regular checking and maintenance to all plants at site. 5) RSS has replied to the complainant on the arrangement of the measures taken on 17 October 2011. Complainant was satisfied with the response and follow-up action taken by the Contractor.	Closed
111104	04/11/2011	Mr. Liu from	Wan Chai	Complain about a tree near the	1) ET confirmed with the Resident Site Staff that	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		LCSD complained via Contractor Complaint Hotline		site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road, the status is not healthy and roof ball of two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue were half cut.	- A tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road is the Tree no. TA1122 under Contract no. HK/2009/02. Leaves of a branch of this tree were shrivelled. - Two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue are the tree nos. A160 and A161 under Contract no. HK/2009/01. Part of roof ball of these two trees was covered by the metal plate. 2) Independent Tree Specialists for these two inspected the trees. Contractor HK/2009/01 has taken the measure as recommend downgrading the soil level around the trunk base. Reinstating of the ground works will be conducted in mid-December 2011. For the tree no. TA1122 under Contract no. HK/2009/02, the brown leaves were removed and fenced the tree with orange net is provided to prevent damage of tree trunk by construction works. The distance between the tree and the edge of the trench is kept approximate 2m. Two Contractors were reminded to carry out regular watering to the trees within their site area.	
111106	06/11/2011	Police officer	Wan Chai	Construction noise generated from the site at about 6:30 a.m on 6 November 2011 and require to stop the machine operation	1) According to the information reported by Contractor, one BC cutter and hoist were operated for Diaphragm Wall construction of Shatin-Central Link to inspect bentonite pipes and ensure no damages and all the joints are tightened in good position. Then, the subcontractor for Diaphragm wall, SAMBO Korean foreman stopped the engine of the BC cutter immediately. The police officer recorded the details and HKID number of the foreman and then left. Due to the different language communication between the police officer and the Korean foreman, no CNP was checked by the police officer. 2) ET confirmed with the Resident Site Staff that same issue was also raised out by RSS at about 7:00a.m on the same day. Besides, it was confirmed that there is no valid Construction Noise Permit for the conducted construction works in the period between 2300 and 0700. 3) Due to insufficient communication between Contractor HK/2009/01 and their Korean Sub-contractor, Korean Sub-contractor had not notified to Contractor before carrying out the inspection of the BC cutter, hoists and	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					bentonite pipes at about 6:00a.m to ensure no damages and all the pipe joints should be tightened and in good position. 4) Contractor was advised to enhance the communication between Contractor and sub-contractor and provide sufficient environmental training to all foreman and operators on restricted hour operation. Furthermore, Construction Noise Permit should be checked and in place for the construction works during restricted hour 5) This complaint was considered in relation to the conducted construction works during restricted hours without valid Construction Noise Permit. No more construction works were conducted during night time period. The construction works will be conducted in accordance with the time period stated in valid CNP. This complaint will be kept in view of any follow-up action from the relevant government activities.	
111212	12/12/2011	The complainant, Mr Tsui from IFCII's management office complained via hotline 1823	Central	A visual impact complaint from hotline 1823 was received by ET on 9 January 2011 (ICC Ref. No.: ICC#1-333037096 dated on 12 December 2011). The complaint, Mr Tsui was reported that visual nuisance caused by lighting in the construction site during night time.	1) RSS notified ET on 9 Jan 2012. 2) ET confirmed with the Resident Site Staff that A joint inspection was conducted by Mr Tsui and contractor on that night to see whether there is any improvement. 3) Due to safety reason, igniting enough lights should not be avoided in construction site. However, the light sources were not directed away from pointing to the sensitive receiver and results in visual glare to the complaint. 4) Confirmed with the Resident Site Staff the complainant was satisfied the new arrangement of the lights with contractor after the joint inspection. No further complaint received after that.	Closed
111220	20/12/2011	The complainant, Ms. Poon complained via hotline 1823 (ICC Ref. No.: ICC#1-334683841)	North Point	Construction air and noise nuisance generated that many trucks carrying construction materials driving along Watson Road and Oil Street and possibly entering/leaving the construction site near the IEC during 0800 to 1900 hours.	1) RSS notified ET on 22 Dec 2011. 2) ET confirmed with the Resident Site Staff that the complainant cannot identify whether the trucks were working under the CWB project or not. 3) The dominant construction air and noise nuisances were emitted by the trucks along Oil Street and Waston Road, however, this is the public road for all vehicles. Reviewing the air quality monitoring and noise monitoring results. No exceedance was recorded during this period. 4) Confirmed with the Resident Site Staff that they provided a contact no. for any future enquiries regarding	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					CWB project to the complainant and she was satisfied on the arrangement and no further complaint was received after that.	
111230	30/12/2011	Residents of Harbour Heights	North Point	Construction air and noise nuisance generated by construction vehicles were found parked illegally at King Wah Road and lining up at Oil Street without the engine turning off.	1) RSS notified ET on 6 January 2011. 2) ET confirmed with the Resident Site Staff that a number of construction activities are concurrently proceeding in the vicinity of Oil Street, King Wah Street and a private development project in King Wah Street 3) The dominant construction air and noise nuisances were emitted by the trucks along Oil Street and King Wah Road, however, this is the public road for all vehicles. Reviewing the results of air quality monitoring station (CMA1b) and noise monitoring (M4b). No exceedance was recorded during this period. Site inspections for HY/2009/19 were conducted on 4 January 2012. The condition of the site access at Oil Street and the public road nearby were found satisfactory. It is noted that HyD also allow and encourage their contractors to maximize the use of marine access, where available, to work sites, so as to minimize burdening nearby public roads. When land trips are unavoidable, they require contractors to tidy up their construction vehicles before leaving works sites. No contractor under CWB project parked their vehicles illegally at King Wah Street, and HyD still reminded them not to commit such offence. 4) According to HyD's staff replied the complaint letter on 10 January 2012, there is a private development project under construction at King Wah Road. To access these works sites, construction vehicles have to use public roads nearby. No further complaint received after HyD's reply.	Closed
120118	18/01/2012	N/A	North Point	A complaint regarding a tree located in front of Victoria Centre under IECL was covered by one meter mud without any protection. The complainant concerns the health of the tree in such condition.	1) RSS notified ET on 20 January 2012. 2) ET confirmed with the Resident Site Staff that The tree is inside the site area of HY/2009/19 and The Botanical name of the tree is Ficus superba var. japonica and the I.D. of the tree is UT48 3) According to the information provided by RSS on 20 Jan 2012, the tree shall be felled that has been approved by DLO on 29 August 2011. Moreover, the tree was felled	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					by contractor on 19 January 2012. 4) No further complaint received after HyD's reply.	
120305	03/03/2012	Resident of Harbour Heights complained via hotline 1823 (ICC Ref. No.: ICC#1-344632511)	North Point	A complaint regarding excessive noise from construction sites of CWB was observed outside Harbour Heights from Monday to Saturday before 8am. The plants were frequently turned on before 7:30am creating nuisance. The complainant requested a speedy follow-up and reply from relevant department.	1) RSS notified ET on 5 March 2012. 2) ET confirmed with the Resident Site Staff that PME for diaphragm wall construction started to operate at about 7:30am whilst the other PME, including those for land bored piling work, started to operate after 8am. 3) After reviewing the results of noise monitoring (M4b), no exceedance was recorded during daytime period and the noise level were below 75dB(A). Site inspection for HY/2009/19 was conducted on 7 March 2012. The condition of noise mitigation measures near Harbour Heights was found satisfactory. RSS confirmed that no operation was active before 7:00am everyday. The suspected nuisance was to be considered caused by the PME for diaphragm wall construction. A surprise check was performed on 13 March 2012 by RSS. It was found that no noisy PME was in operation by Contractor of HY/2009/19 before 8am, and the construction noise level was minimal and not disturbing. The noise level and operation time both complied with statutory requirements set up in NCO. 4) Complainant called ICC on 8 March 2012 to confirm HyD has provided a response. No further complaint was received after the response.	Closed
120405	05/04/2012	N/A	North Point	A complaint regarding excessive noise from construction sites of CBTS was observed daily before 7:30am except on public holidays, and the noise source was mainly from piling works. The complainant requested that construction works should start after 8:30am to avoid nuisance to nearby residents and a speedy follow-up and reply.	1) RSS notified ET on 5 April 2012. 2) ET confirmed with the Resident Site Staff that no piling works were performed during the concerned period. 3) After reviewing the results of noise monitoring (M2b and M3a), no exceedance was recorded during daytime period and the noise level was below 75dB(A). Site inspection for HY/2009/15 was conducted on 10 April 2012. The condition of noise mitigation measures around CBTS was found satisfactory. RSS confirmed that no pilings were performed during the concerned period. The major works included drilling, diaphragm wall construction and excavations. 4) HyD made a reply to the complainant on 16 April	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					2012 via 1823. HyD replied that the current works at CBTS were drilling, diaphragm wall construction and deep excavations. In order to minimize the noise generated from the above works, the Contractor had erected temporary noise barriers and provided noise blankets on plants. RSS would continue to work with the Contractor on the effectiveness of the environmental mitigation measures implemented on site. No further complaint was received after the response.	
120415	15/04/2012	The complainant Ms. Law, resident of Fu Lee Loy Mansion, complained via hotline 1823 (ICC Ref. No.: 1-351021108)	North Point	A complaint regarding excessive noise generated from a HyD project that is located at the connection point of CWB and IEC affecting nearby residents. Lately during the middle of the night (around 00:00 to 05:00), low frequency noise, which possibly came from the operating power generator and the barges which were parked along the Oil Street work site, were making a nuisance to the complainant and residents nearby. The complainant requested that relevant department should follow-up.	1) RSS notified ET on 17 April 2012. 2) ET confirmed with the Resident Site Staff that there was no operation of power generators for HY/2009/19 and HY/2009/17 (HY/2009/11 had no physical work on site) during the concerned period. Although there were a few barges mooring at the seafront of HY/2009/19, they were not in operation and hence no operational noise would be emitted. 3) After reviewing the results of noise monitoring (M4b and M5b), no exceedance was recorded during day time period and the noise level was below 75dB(A). Site inspection for HY/2009/19 was conducted on 18 April 2012. The condition of noise mitigation measures near Harbour Heights were found satisfactory. RSS confirmed that no operation of power generators for HY/2009/19 and HY/2009/17 (HY/2009/11 had no physical work on site) during the concerned period. Although there were a few barges mooring at the seafront of HY/2009/19, they were not in operation and hence no operational noise would be emitted. 4) HyD made a reply to the complainant on 30 April 2012 via email. HyD replied that the current works near Oil Street, North Point, included CWB tunnel works, IEC connections and associated foundation works. According to RSS records, no operations were performed during the early hours of March and April at Oil Street and the waterbody nearby, and so it was believed that the noise nuisance was not generated from the CWB project. Despite that, RSS would continue to monitor the Contractor on the operations and effectiveness of the environmental mitigation measures implemented on site, as not to affect daily life of local residents nearby. No further complaint was received after the response.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130308	06/03/2013	ICC Case#1-407181502	Tin Hau	A complaint regarding the dropping of fine rock material into surrounding waterbody was observed during rock breaking operation with two excavators in active operation at the Eastern Breakwater of Causeway Bay Typhoon Shelter near the North Point lighthouse.	1) RSS notified ET on 8 March 2013 2) ET confirmed with RSS that excavation works, installation of buoy, flashing light and silt curtain and dredging works were undertaken at Eastern Breakwater during the concerned period on 6 March 2013. One backhoe equipped with breaker and one derrick barge were confirmed in operation while another backhoe was at idle during the concerned period on 6 March 2013. 3) Reviewing the photo record provided by RSS, the condition of the silt curtain deployed around the Eastern Breakwater on 6 March 2013 was found to be in good condition. It is considered that the silt curtain was properly in place during the concerned period and the concerned act of dropping of fine rock material was confined within the silt curtain boundary without adverse impact to the nearby water quality. Further follow up was conducted on 12 March 2013 during weekly environmental audit inspection, the silt curtain deployed around the concerned area was found to be maintained in good condition and the water quality at the concerned work area was generally satisfactory. No violation of the Environmental Permit condition was found. The contractor was advised and committed to implement preventive measures to minimize the potential impact of work including conducting regular diver check to ensure the integrity and the extend of silt curtain deployment and to provide adequate back up stock of silt curtain for emergency use.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130606	30/5/2013	ICC Ref. No.: #1-430164728	Central – Man Kat Street	1. A number of trees (approximately more than ten) along Man Kat Street were found to be in poor health condition with withered and yellow leaves. The complainant has requested a follow-up by relevant department.	1) RSS notify ET on 6 June 2013 2) ET confirmed with the Resident Site Staff that According to the information provided by RSS, 13 no. of the trees - Roystonea regia (T1674, T1675, T1676, T1677, T1678, T1679, T1680, T1681, T1683, T1644, T1643, T1641, T1639) at the concerned location raised by the complainant was found to be with withered and yellow leaves and 1 no. of tree- Khaya senegalensis (T1712) raised by the complainant was found to be in poor health condition. No construction works was undertaken by Contract HY/2009/18 at the concerned planter area where the affected trees are located. It was also observed that an active CEDD construction works area under a separate contractor not related to Central Wan Chai Bypass Project was found to be located within the concerned planter area. 3) A follow-up joint inspection with RSS and Landscape specialist was conducted on 10 June 2013, it was considered that the withered and yellow leaves of the affected trees (T1674, T1675, T1676, T1677, T1678, T1679, T1680, T1681, T1683, T1644, T1643, T1641, T1639) at the concerned planter area were contributed by natural life cycle of the affected trees and the health condition of the affected trees were considered to be fair. It was also noted that an active CEDD works area was located within the concerned planter area in close proximity to few of the concerned trees (T1644, T1643, T1641, T1639) According to tree inspection records from Jan 2013 to May 2013 confirmed by RSS (Document Ref: CI-F1-043b, CI-F1-044b, CI-F1-045b, CI-F1-046b, CI-F1-047b), the affected tree (T1712) at the concerned planter area was considered to show sign of withering and considered to be in poor health condition in latest tree survey report confirmed by RSS.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					During the follow-up inspection on 10 June 2013, It was observed that construction material and oil drum were placed near the the roots area of other trees within the CEDD works. Despite the above observation, no direct evidence was found on site which indicates the work front have contributed to the poor health condition of the affected tree (T1712) at the time of investigation. 4) The relevant contractor have removed the construction material near the root area of the trees retained on site and conduct pruning to remove the withered and yellow leaves retained on tree trunk to minimize impact on the trees appearance.In addition, safety supporting wire was provided for concerned tree (T1712) 5) ET recommended the contractor to keep in view the health condition of the concerned tree (T1712) and apply permission for tree felling together with tree compensation plan if considered necessary. Furthermore, the contractor was reminded to implement regular checking of tree health condition and regular removal of withered leaves to maintain the overall tree appearance.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130611	30 May 2013 and 1 June 2013	EPD Ref.:H04/RS/0001 1587-13	Area near Central Pier	1. Noise was emanated from the construction site near the Central Piers at around 0900 hrs on 30 May 2013 and other days and requested follow up action by relevant department.	1) RSS notify ET on 11 June 2013 2) ET confirmed with the Resident Site Staff that According the information confirmed by RSS, major noise generating construction activities undertaken at works area near Central Pier during the concerned time include - Breaking up existing D-wall concrete and excavation at portion 4B and 4C - Sheet piling works at Portion VI (Man Kat Street) 3) Total 1 no. of Backhoe with breaker, 1 no. of Backhoe with vibratory hammer and 4 no.s of pneumatic breakers were deployed for the above construction activities. Reviewing the noise monitoring data at monitoring stations (M7e- International Finance Centre Eastern End of Podium and M7w- International Finance Centre Western End of Podium), no limit level exceedances were recorded during routine noise monitoring event on 28 May 2013 and 03 June 2013. As similar construction works activities conducted on 30 May 2013 was continued across the above monitoring period, the noise emanated from the construction activities under Contract HY/2009/18 was considered to complied with the statutory requirement. In addition, weekly environmental site inspection was conducted on 30 May 2013 at around 10:00. According to the inspection record, no particular observation regarding noise impact was recorded and the mitigation measures including erection of of temporary noise barrier was observed in place. As such, no direct information associated with the noise concerned raised was considered available and no non-conformity was identified. 4) ET recommend the contractor to review the need of additional noise mitigation measures to further reduce the noise enmated during construction works for pier side public area.	Interim report submitted to EPD on 19 June 2013, EPD advised no further comment on 5 Aug 2013 and final report for case closing submitted on 6 Aug 2013.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
131010	03 Oct 2013	ICC Ref: No.1-467000768	Area between Central Pier and International Finance Centre	Noise and air quality impact was experienced at the area located between IFC and Central Pier during peak hours.	ET confirmed with the Resident Site Staff that 1) The major construction activities at the concerned location conducted over the past three months include; - Formwork, rebar and concreting - Backfilling - Water-proofing - Scaffolding erection 2) Mitigation measures implemented by the Contractor for the above construction works include - Select quiet plant and work methods; - Check plant and equipment for condition; - For use of powered mechanical equipment during restricted hours: Obtain necessary Construction Noise Permit and strictly comply with their conditions; - Frequently spray water to major haul road and stockpiles to suppress dust generation; and - Cover stockpiles with impervious sheets The construction activities including backfilling, concreting and other associated tunnel works were undertaken in the past three months. Having reviewing the monitoring data of the monitoring stations in the vicinity of the concerned location raised by the complainant, namely monitoring station M7e and M7w (Noise Monitoring Station) and MA1e and MA1w (Air Monitoring Station), no action or limit level exceedance was recorded. In addition, mitigations measures including water spraying and erection of noise barrier were observed during weekly site inspection in August and September 2013 and reminders on dust mitigations measures given during weekly site inspection to the contractor were rectified. As such, the construction activities under Contract HY/2009/18 were considered in compliance with the statutory requirement and no cumulative air/ noise quality impact was observed in the past three months.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Elevated noise level at monitoring station M7e (International Finance Centre East Podium) was noted on 24 September 2013. The Contractor is recommended to review the current measures and to implement additional noise mitigation measures to further avoid potential impact to nearby public area during construction works.	
131217	16 Dec 2013	ICC Case Ref.: 1-484998552	Victoria Park near Hing Fat Street Exit	Sweeping of muddy water into public drains.	ET confirmed with the Resident Site Staff that 1)The major construction activities around the concerned location conducted on 16 Dec 2013 a.m.includes: -Preparation work of rootball for tree transplanting According to the information provided by RSS, the construction activities around the concerned location on 16 Dec 2013 include preparation work of rootball for tree transplanting at Zone 17/18. A further investigation on the complaint was conducted on 19 Dec 2013 during weekly environmental inspection. It was observed that a tree worksarea comprised of mainly loosen soil was located near the concerned location. It was considered that the inclined surface and loosen soil nature of the concerned worksarea could have led to the muddy surface runoff in rain. Deposition of muddy runoff onto nearby public pavement outside worksarea was hence resulted and was subsequently cleaned into nearby public stormwater drain by the Contractor's workers on the complaint date. As such, the case was considered as works related. Sandbags, geotextile and gravels were immediately placed by the Contractor around the gullies at the concerned location to prevent leftover muddy runoff to the public stormwater drain as observed during the weekly inspection on 19 Dec 2013. With respect to the follow-up raised by the complainant on 19 Dec 2013, sandbags, geotextile and gravels placed at gullies located at public area were removed by the Contractor on the same day for maintaining passible public pavement. Follow up measures including sandbag bundle and covering of worksarea with impervious sheeting was immediately placed at the source of impact at the concerned worksarea boundary by the Contractor.	Final investigation report issued on 20 Dec 2013. Case closed on 3 Jan 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
131224	24 Dec 2013	(ICC Case Ref.: 1-486434321	Victoria Park Children Playground	Odour and large amount of dust particles affecting the public user of the Victoria Park near Children playground	ET confirmed with the Resident Site Staff that 1) The major construction activities around the concerned location conducted on 24 Dec 2013 include: - Breaking up existing pillar box for new children playground Portion II - Pressing of sheet pile at bowling green for ELS works Portion XII - Welding work for preparation of sheetpiling work at bowling green Portion VI - Demolition of existing pavilion for bowling green Portion VI - Felling of tree TA50 at Victoria Park Zone 2) Mitigation measures implemented by the Contractor for the above construction works include - Water spraying for demolition and other dust generating works. According to the relevant site records, breaking up of existing pillar box, pressing of sheet pile, welding work for preparation of sheetpiling demolition of existing pavilion and felling of tree TA50 at Victoria Park Zone 13 were conducted at the concerned location during the time of complaint. Based on information and photo record provided by the RSS, dust mitigation measures including water spraying during dust generating works were implemented by the Contractor at the concerned location on 24 Dec 2013. Follow-up investigation was conducted on 27 Dec 2013 during weekly environmental inspection, dust mitigation measures including water spraying to dusty area and major dust generation works were confirmed in place despite a general reminder was given to the contractor to enhance the water spraying to dusty haul road during dry season. Based on on-going site inspection and the follow-up investigation, the site condition was considered generally satisfactory and no non-conformance was identified. Upon further review on the supplementary information provided by the complainant on 31 Dec 2013 and investigation conducted on 2 Jan 2014, the tree felling work of tree TA50 was located nearest to the location of the complainant. According to the location plan provided by the RSS and on site investigation, the tree felling work	Case closed and full investigation report issued on 3 Jan 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					for TA50 was immediately in front of the location of the complainant. Based on site observation, scrap material of bark and leaves inevitably generated from cutting of branches during tree felling work was considered to be the most probable cause for the observation raised by the complainant at the concerned location on 24 Dec 2013. Furthermore, welding work was observed near the concerned location and was considered to be the potential source for the smell and exhaust fumes as described by the complainant. Notwithstanding the above, welding work was not identified as a work activity with air quality impact under Project EIA report but it would be desirable to implement preventive measures to minimize potential nuisance to nearby public.	
140123	22 Jan 2014	ICC Case Ref.:1-494077682	Causeway Bay Typhoon Shelter	Construction works have been undertaken during restricted hours until 2300 hrs and occasionally the working hours were extended to around 0100 hrs at nighttime period over the last two to three months at a construction site located within Causeway Bay Typhoon Shelter. For instance, concreting and excavation works were conducted at the concerned location on 22 Jan 2014 during nighttime hours and generated noise impact to the complainant.	ET confirmed with the Resident Site Staff that No construction activity was undertaken at workzone TS1 under HY/2009/15 within Causeway Bay Typhoon Shelter after 1900 hrs on 21 Jan 2014. No construction activity was undertaken at workzone TS3 under HY/2010/08 within Causeway Bay Typhoon Shelter after 1900 hrs on 21 Jan 2014. Concreting for base slab and hanger wall was conducted at workzone TS2 under HY/2009/15 within Causeway Bay Typhoon Shelter from 1900 to 0000 hrs on 21 Jan 2014; Total 8 no.s of concrete lorry mixers, 1 no. of water pump, 2 no.s of concrete pumps (lorry mounted), 1 no. of mobile crane QPME (diesel) and 3 no.s of vibratory pokers were operating from 1900 to 0000hrs on 21 Jan 2014. Concreting for base slab and hanger wall was conducted at workzone TS2 under HY/2009/15 within Causeway Bay Typhoon Shelter from 0000 to 0700 hrs on 22 Jan 2014; Total 1. no of concrete lorry mixer, 1 no. of water pump, 1 no. of concrete pump (lorry mounted), 1 no. of vibratory poker were operating from 1900 to 0000hrs on 22 Jan 2014	Case closed and full investigation report issued on 4 Feb 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to the relevant site records, from 1900-0000hrs on 21 Jan 2014, concreting for base slab and hanger wall was conducted at workzone TS2 under HY/2009/15 within Causeway Bay Typhoon Shelter. Total 8 no.s of concrete lorry mixers, 1 no. of water pump, 2 no.s of concrete pumps (lorry mounted), 1 no. of mobile crane QPME (diesel) and 3 no.s of vibratory pokers were operating at the above period. From 0000 to 0700 hrs on 22 Jan 2014, concreting for base slab and hanger wall was conducted at workzone TS2 under HY/2009/15 within Causeway Bay Typhoon Shelter. Total 1. no of concrete lorry mixer, 1 no. of water pump, 1 no. of concrete pump (lorry mounted), 1 no. of vibratory poker were found operating at the above period. After reviewing relevant photo records and information verified by RSS and the Construction Noise Permit (CNP) no.GW-RS1384-13, it was considered that several conditions of CNP GW-RS1384-13 were not fulfilled by the Contractor in particular for the item(s) below, No acoustic installation was provided for the relevant PME(s) used as stated in CNP condition 3.d.during the concerned concreting works. From 1900 to 2300 hours on 21 Jan 2014, the PME(s) used on-site did not comply with any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in CNP no.GW-RS1384-13. From 0000 to 0700 hours on 22 Jan 2014, the PME(s) used by the Contractor on-site did not comply with any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in CNP no.GW-RS1384-13. From 1900 to 2300 hours on 21 Jan 2014 and from 0000 to 0700 hours on 22 Jan 2014, PME (Concrete Lorry Mixer) was deployed by the Contractor without barge enclosure and was unable to comply with condition 3.a. in CNP no.GW-RS1384-13.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
140127	24 Jan 2014	ICC Case Ref.: 1-494612639	Works area adjacent to the Victoria Park Bowling Green	Noise generated from piling works conducted at the works area adjacent to the Victoria Park Bowling Green have created nuisance to the Bowling Green users.	ET confirmed with the Resident Site Staff that The major construction activities around the concerned location conducted on 23 Jan 2014 include: Pressing of sheetpile Ch.279-285 (RHS) and Ch.317 for ELS works on 23 Jan 2014. Splicing of sheetpile Ch.275-285 (LHS) for ELS works on 23 Jan 2014. Mitigation measures implemented by the Contractor for the above construction works include: Installation of acoustic panels along hoarding line at East Bowling Green; Installation of addition noise barriers on top of hoarding at East Bowling Green; Display of publicity notices along hoarding line; and No noisy work shall be carried out at the areas adjoining East Bowling Green as if there is any Bowling Green competition event to be held (i.e. Saturday afternoon). According to relevant site records, pressing of sheetpile Ch.279-285 (RHS) and Ch.317 for ELS works and splicing of sheetpile Ch.275-285 (LHS) for ELS works were conducted at the concerned location during the time of complaint. Based on the photo records and information verified by RSS, noise mitigation measures including installation of acoustic panels along hoarding line at East Bowling Green and installation of addition noise barriers on top of hoarding at East Bowling Green were implemented by the Contractor at the concerned location. Furthermore, no noisy work was conducted by contractor at the areas adjoining	Case closed and full investigation report issued on 6 Feb 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					East Bowling Green when there is any Bowling Green competition event to be held. Follow-up investigation was conducted on 29 Jan 2014 during weekly environmental inspection, noise mitigation measures including noise barriers and acoustic panels were confirmed in place and maintained in good condition. According to previous environmental inspections recorded in Jan 2014, no particular observation regarding the noise impact was recorded. As such, no non-conformity was identified.	
140311	27 Feb 2014	EPD Complaint Case (Ref:H04/RS/00 04232-14) received by ET on 11 March 2014	Central IFC Area	Excessive noise (from the operation of compressors, other heavy machinery and concrete breaking) was emanated from the construction site near IFC in daytime on 27 Feb 2014.	ET confirmed with the Resident Site Staff that The major construction activities at the concerned location conducted on 27 Feb 2014 (Daytime) include: Backfilling works between north wall and sheetpiles and for roof slab; Site hoarding removal; Formwork erection and removal works, falsework erection; Concrete breaking works at roof slab and base slab and breaking up of existing tunnel corner; Concreting works for profile barrier inside cut and cover tunnel; and Rebar fixing works and WVB basement remediation works. Mitigation measures implemented by the Contractor for the above construction works include: Use of quiet plants (air compressor with a Noise Emission Label of 99 dB(A)).	Interim report submitted to EPD on 18 March 2014, EPD advised no further comment on 26 March 2014 and final report for case closing issued on 26 March 2014



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to relevant site records, major noise emanating construction activities conducted around the concerned location on 27 Feb 2014 include concrete breaking works at roof slab and base slab and breaking up of existing tunnel corner and concreting works. Based on information verified by the RSS, noise mitigation measure including utilization of quiet air compressor with noise emission label of 99 dB(A) was implemented by the Contractor on the 27 February 2014 to minimize the potential noise impact. Having reviewed the monitoring data of the monitoring stations in the vicinity of the construction site near IFC, namely noise monitoring stations M7e and M7w, no limit level exceedances were recorded on 24 Feb 2014 and 4 March 2014 and the major concrete breaking works at the concerned location conducted on 27 February 2014 was continued across the above monitoring period. In addition, no particular observations regarding noise impact were recorded during weekly site inspection conducted on 27 Feb 2014. No non-conformity was identified. As such, the construction activities under Contract HY/2009/18 were considered generally in compliance with the statutory requirement. Nevertheless, in view of the concern regarding noise nuisance raised by public, it is considered desirable for the Contractor to review and strengthen the noise mitigation measures around the concerned location. Follow-up inspection was conducted during weekly environmental inspection on 13 March 2014, additional noise mitigation measure including erection of noise blanket for concrete breaking works were implemented by the Contractor to further minimize the noise nuisance to nearby public	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
140623	11 June 2014	EPD Complaint Case (Ref:H04/RS/00 013590-14) received by ET on 23 June 2014	Foot Bridge to Central Pier 7	Excessive Paint Spray Odour	A public complaint regarding odour concern referred by EPD was received by ET on 23 June 2014. The complainant reported that excessive paint spray odour was detected at the foot-bridge to the Central Pier 7. ET confirmed with the Resident Site Staff that spraying of waterproofing membrane (integritank) from Ch1700 to Ch1705 was conducted at roof slab Bay12 on 11 June 2014 and Screeding concrete placing from Ch1700 to Ch1683 was conducted at roof slab Bay12 on 11 June 2014 and Backfilling and removal of concrete blocks was conducted at roof slab Bay 11 and Bay 10-north on 11 June 2014 According to relevant site records, major construction activities conducted around the concerned location on 11 June 2014 include spraying of waterproofing membrane (integritank) from Ch1700 to Ch1705; screeding concrete placing from Ch1700 to Ch1683 and backfilling and removal of concrete blocks. Having reviewed the relevant information verified by RSS, the chemicals applied at the concerned area on 11 June 2014 are waterproof paint and paint adhesives. In view of the concern regarding odour nuisance raised by the public, it is considered desirable for the Contractor to review the application method for waterproof layer nearby public area to minimize the nuisance caused to the surroundings.	Preliminary report issued on 25 June 2014. Interim report submitted to EPD on 30 June 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up inspection was conducted during weekly environmental inspection on 26 June 2014, no further spraying works was conducted by the Contractor at the concerned area and no particular odour was observed at the concerned location.	
20140723	21 July 2014	ICC complaint (ICC Case Ref.: 2-341537112) received by ET on 23 July 2014	Area opposite to Ngan Tao Building	Noise nuisance due to works and machine at opposite project site during nighttime	A public complaint regarding construction noise impact referred by RSS was received by ET on 25 July 2014 (ICC Case Ref.: 2-341537112 dated 21 July 2014). The complainant reported that : At 00:57hrs on 21 July 2014, he could not sleep due to work and machine at the project site opposite to the building (Ngan Tao Building), where he was living, were still going on and in operation. Noise traveled to his flat despite it was some distance away. ET confirmed with the Resident Site Staff that dewatering works was conducted under HY/2009/19 at the works area at Watson Road from around 23:00hrs on 20 July 2014 to 01:00hrs on 21 July 2014. Total 1 no. of generator and 23 nos. of dewatering pumps were in operation. Mobilization of telescopic arm excavator to trailer truck was performed under HY/2009/19 at the works area at Watson Road from around 00:15hrs to 01:00hrs on 21 July 2014. Total 1 no. of telescopic arm excavator and 1 no. of trailer truck were in operation. According to the relevant site records under Contract HY/2009/19, from around 23:00hrs on 20 July 2014 to 01:00hrs on 21 July 2014, dewatering works was conducted under HY/2009/19 at the works area at Watson Road. Total 1 no. of generator and 23 nos. of dewatering pump were in	Final Investigation report (Issue1) issued on 31 July 2014. Final investigation report (Issue 2) based on further follow-up issued on 12 Aug 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					operation at the above period. In addition, mobilization of telescopic arm excavator to trailer truck was performed under HY/2009/19 at the works area at Watson Road from around 00:15hrs to 01:00hrs on 21 July 2014. Total 1 no. of telescopic arm excavator and 1 no. of trailer truck were in operation. After reviewing relevant records and information verified by RSS and the Construction Noise Permit (CNP) no. GW-RS0152-14, it was considered that the below condition of CNP no.GW-RS0152-14 was not fulfilled by the Contractor of HY/2009/19. From 00:15hrs to 01:00hrs on 21 July 2014, the PME(s) (1 no. of telescopic arm excavator and 1 no. of trailer truck) operated under the Contractor of HY/2009/19 on-site could not follow any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in no.GW-RS0152-14. Notwithstanding the above, according to the information provided by the RSS, the telescopic arm excavator was mobilized at night time hours with consideration that passage of vehicle with large plant & machinery through cross harbour tunnel shall be conducted after mid-night. the Contractor of HY/2009/19 was advised to review the need to renew relevant CNP for PME grouping with respect to specific site operation requirements such that the Construction Noise Permit would be followed. Furthermore, the Contractor of HY/2009/19 was suggested to review the arrangement for PME mobilization with maintenance need to be conducted within specific period allowed under the relevant CNP(s).	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20140801	30 July 2014	ICC complaint (ICC Case Ref.: 2-360638977) received by ET on 01 August 2014	Area opposite to Harbour Heights	Noise of sand and gravel movements at area opposite to the Harbour Heights	A public complaint regarding construction noise impact referred by RSS was received by ET on 01 Aug 2014 (ICC Case Ref.: 2-360638977 dated 31 July 2014). The complainant reported that at 01:20hrs on 30 July 2014, the complainant was woken up by the noise of sand and gravel movements at area opposite to the Harbour Heights. ET confirmed with the Resident Site Staff that EVB excavation was undertaken at the works area around Watson Road under HY/2009/19 before 23:00hrs on 29 July 2014. (Total 1 no. of excavator, 1 no. of dump truck, 23 nos. of underground dewatering pump and 3 nos. of generator were in operation). Dewatering works was undertaken at works area around Watson Road under HY/2009/19 from 23:00hrs on 29 July 2104 to 01:00 hrs on 30 July 2014. (Total 23 nos. of underground dewatering pumps and 1 no. of generator were in operation). Mobilization of PMEs was performed at works area around Watson Road under HY/2009/19 from 00:45hrs to 01:30hrs on 30 July 2014. (1 no. of excavation machine and 1 no. of dump truck were in operation). No other construction activity or operation was performed at the area opposite to Harbour Heights from 23:00hrs on 29 July 2014 to 01:00hrs on 30 July 2014 under HY/2009/19. According to the relevant site records, before 2300hrs on 29 July 2014, EVB excavation at the works area around Watson Road was conducted under HY/2009/19. (Total 1 no. of dump truck , 1 no. of excavator, 3 nos. of generators and 23 nos. of dewatering pumps were in operation at the	Final investigation report issued on 12 Aug 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					above period). From around 23:00hrs on 29 July 2014 to 01:00hrs on 30 July 2014, dewatering works at works area around Watson Road was conducted under HY/2009/19. Total 23 nos. of dewatering pumps were operating at the above period. In addition, mobilization of PMEs was performed at works area around Watson Road under HY/2009/19 from 00:45hrs to 01:30hrs on 30 July 2014. Total 1 no. of excavation machine and 1 no. of dump truck were in operation. After reviewing relevant records and information verified by RSS and the Construction Noise Permit (CNP) no. GW-RS0152-14, it was considered the below condition of CNP GW-RS0152-14 was not fulfilled by the Contractor of HY/2009/19. From around 00:45hrs to 01:30hrs on 30 July 2014, the operation of PME(s) (1 no. of excavator and 1 no. of dump truck) under the Contractor of HY/2009/19 on-site could not follow any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in no. GW-RS0152-14. Notwithstanding the above, according to the information provided by the RSS, the excavator and dump truck were mobilized away from the edge of the temporary ELS structure towards the area opposite to the Harbour Heights after 23:00hrs under safety consideration. The Contractor of HY/2009/19 was advised to review the arrangement and location for retaining and securing PME(s)/ plants to minimize the movements of PME or plants after completion of works such that the Construction Noise Permit would be followed.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20140929	26 Sep 2014	ICC complaint (ICC Case Ref.: 2-466911619) received by ET on 29 September 2014	IEC flyover opposite to City Garden	Light originating from the flyover under Central-WanChai Bypass Project was emitted towards City Garden direction and caused light nuisance	A public complaint regarding visual impact referred by RSS was received by ET on 29 September 2014 (ICC Case Ref.: 2-466911619 dated 26 September 2014) The complainant reported that on 26 September 2014 at around 00:50hrs, light originating from the flyover under Central-WanChai Bypass Project was emitted towards City Garden direction and caused light nuisance. ET confirmed with the Resident Site Staff that the light emission on 25 and 26 September 2014 at the concerned area was originated from the temporary lighting provided at the soffit of the permanent noise enclosure at the new Island Eastern Corridor (IEC) Eastbound which was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after the traffic diversion on 28 September 2014. According to the relevant information provided by RSS, the light emission on 25 and 26 September 2014 at the concerned location was originated from the temporary lighting provided at the soffit of the permanent noise enclosure at the new Island Eastern Corridor Eastbound. The lighting was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after traffic diversion on 28 September 2014. Nevertheless, in view of the public concern regarding light nuisance raised by the public, it is considered desirable for the Contractor to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surrounding receivers as far as practicable.	Final Investigation report submitted on 9 October 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up inspection was conducted during weekly environmental inspection on 8 October 2014, additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance caused to the surroundings. Further to the interim measure implemented by the Contractor of HY/2009/19, the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings. The Contractor of HY/2009/19 was suggested to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surroundings receivers as far as practicable. Additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance caused to the surroundings and the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20141006	25,26 Sep 2014	ICC complaint (ICC Case Ref.: 2-469099657) received by ET on 06 October 2014	IEC flyover opposite to City Garden	Light originating from the flyover under Central-WanChai Bypass Project was emitted towards City Garden direction and caused light nuisance	A public complaint regarding visual impact referred by RSS was received by ET on 6 October 2014 (ICC Case Ref.: 2-469099657 dated 26 September 2014). The complainant reported that on 25 September 2014 night and on 26 September 2014 at around 23:23 hrs, light originating from the flyover under Central-Wan Chai Bypass Project was emitted towards City Garden direction and caused light nuisance. ET confirmed with the Resident Site Staff that the light emission on 25 and 26 September 2014 at the concerned area was originated from the temporary lighting provided at the soffit of the permanent noise enclosure at the new Island Eastern Corridor (IEC) Eastbound which was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after the traffic diversion on 28 September 2014. According to the relevant information provided by RSS, the light emission on 25 and 26 September 2014 at the concerned location was originated from the temporary lighting provided at the soffit of the permanent noise enclosure at the new Island Eastern Corridor Eastbound. The lighting was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after traffic diversion on 28 September 2014. Nevertheless, in view of the public concern regarding light nuisance raised by the public, it is considered desirable for the Contractor to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surrounding receivers as far as practicable.	Final Investigation report submitted on 9 October 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up inspection was conducted during weekly environmental inspection on 8 October 2014, additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance caused to the surroundings. Further to the interim measure implemented by the Contractor of HY/2009/19, the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings. The Contractor of HY/2009/19 was suggested to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surroundings receivers as far as practicable. Additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance caused to the surroundings and the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20141010	07 Oct 2014	ICC complaint (ICC Case Ref.: 2-487376144) received by ET on 10 October 2014	IEC flyover opposite to City Garden	Light originating from the flyover under Central-WanChai Bypass Project was emitted towards City Garden direction and caused light nuisance	ET confirmed with the Resident Site Staff that temporary lighting was provided at the concerned area at the soffit of the permanent noise enclosure at the new Island Eastern Corridor (IEC) Eastbound which was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after the traffic diversion on 28 September 2014. Temporary lighting was provided at the concerned area at the soffit of the permanent noise enclosure at the new Island Eastern Corridor (IEC) Eastbound which was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after the traffic diversion on 28 September 2014. In view of the public concern regarding light nuisance raised by the public, it is considered desirable for the Contractor to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surrounding receivers as far as practicable. During weekly environmental inspection on 8 October 2014, additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance caused to the surroundings. Further to the interim measure implemented, on 13 October 2014 the Contractor of HY/2009/19 have replaced the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings.	Final investigation report submitted on 14 Oct 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					The Contractor of HY/2009/19 was suggested to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surroundings receivers as far as practicable. Additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure and on 13 October 2014 the Contractor of HY/2009/19 have replaced the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings.	
141016	14 Oct 2014	EPD complaint EPD Ref.:H05/RS/00 025795-14) received by ET on 16 October 2014	work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	Construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	A public complaint regarding construction noise impact referred by EPD was received by ET on 16 October 2014 (EPD Ref.: EP860/E2/24 Annex IV dated 16 October 2014). The complainant reported that construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground. ET confirmed with the Resident Site Staff that From 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.	Updated interim investigation with supplementary information submitted to EPD on 17 November 2014. EPD advised no further comment on the updated interim report and case closed on 27 Nov 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02. From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway. Total one scissor platform and two hand held drills (battery) were in operation. From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road. Total one crane lorry was in operation. According to the relevant site records under Contract HK/2009/02, from 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02. From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway. Total one scissor platform and two hand held drills (battery) were in operation. From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road. Total one crane lorry was in operation. In view of the above findings, no direct information associated with the noise concern was considered available.	
20141108	07 Nov 2014	EPD complaint (EPD Ref.: H05/RS/00027 815-14) received by ET on 10 November 2014	Construction site at old Wan Chai Ferry Pier	Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool.	A public complaint regarding odour concern referred by EPD was received by ET on 07 November 2014 (EPD Ref.: H05/RS/00027815-14 dated 10 November 2014). The complainant reported that Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool. ET confirmed with the Resident Site Staff that ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool). Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated. Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.	Interim investigation report submitted to EPD on 17 November 2014. EPD advised no comment on the interim report and case closed on 1 Dec 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Dredging works was conducted on 7 November 2014 during daytime at WCR3 (East of old Wan Chai Ferry Pier) Total 1 no. of dredger, 1 no. of hopper and 1 no. of tug boat were operated. According to the relevant site records under Contract HK/2009/02, ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool). Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated. Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated. Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site. The condition of chemical waste storage was considered satisfactory and no malodour was identified. Despite no information related to malodour was identified, the Contractor was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site. Based on the relevant information provided by RSS, despite no information associated with the malodour concern was identified after investigation, the Contractor was reminded to conduct regular checking on the condition of PME used on site to ensure only well maintained PME are used on site The interim report would be submitted to EPD on 17 November 2014.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20141113	12 Nov 2014	EPD complaint (EPD Ref.: H05/RS/00028 253-14) received by ET on 13 November 2014	Construction site at old Wan Chai Ferry Pier	Malodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians.	A public complaint regarding odour concern referred by EPD was received by ET on 13 November 2014 (EPD Ref.: H05/RS/00028253-14 dated 13 November 2014). The complainant reported that Malodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians. (Contract HK/2009/02) ET confirmed with the Resident Site Staff that demolition works was conducted under Contract HK/2009/02 on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated. According to the relevant site records under Contract HK/2009/02, demolition works was conducted on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated. In addition, investigation found that due to malfunctioning of one of the excavators deployed at old Wan Chai Ferry Pier, dark smoke was emitted from the defective excavator for a short period of approximately 30 seconds at around 15:00 hrs on 12 November 2014. The operation of excavator was immediately suspended and followed by repair works. The normal operation of the excavator was resumed after repair. Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site and the Contractor of HK/2009/02 was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.	Interim investigation report submitted to EPD on 19 November 2014. EPD advised no comment on the interim report and case closed on 8 Dec 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20150127	21 Jan 2015	EPD complaint (EPD Ref.: H05/RS/00001 725-15) received by ET on 27 January 2015 and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015	A portion of Hung Hing Road immediately to the east of Marsh Road near SPCA	Construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public.	A public complaint regarding air quality impact referred by EPD was received by ET on 27 January 2015 (EPD Case Ref.: H05/RS/00001725-15 dated 27 January 2015) and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015. The complainant reported that construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public. ET confirmed with the Resident Site Staff that the major construction activities around the concerned location conducted on 21 January 2015 include breaking of seawall blocks and D-wall at TPCWAW; concreting, grouting and drilling works at TPCWAW;reclamation/ backfilling works at TPCWAW Mitigation measures implemented by the Contractor for the above construction works include spraying haul road with water; covering bagged cement with tarpaulin; providing three sided and top covering for grouting stations; providing water spraying to dusty activities such as breaking works According to the relevant site records, breaking of seawall blocks and D-wall, concreting, grouting and drilling works and reclamation/ backfilling works were conducted at TPCWAW. Dust mitigation measures including spraying haul road with water, covering bagged cement with tarpaulin, providing three sided and top covering for grouting stations and water spraying to dusty activities such as breaking works were implemented by the Contractor of HY/2009/15 near the concerned location on 21 January 2015.	Interim report submitted to EPD on 9 February 2015, EPD advised no comment on 27 February 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up investigation was conducted on 27 January 2015 during weekly environmental inspection, dust mitigation measures including water spraying for dusty haul road and major dust generation works; and provision of three sides and top covering for grouting station were confirmed in place. In addition, based on the review of the monitoring data of the monitoring station located at the concerned location raised by the complainant, namely monitoring station CMA3a , no action or limit level exceedance was recorded during air quality monitoring conducted on 20 and 21 January 2015. Nevertheless, the Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on the complaint date was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants. As such, the site condition under Contract HY/2009/15 at the concerned location was considered to be generally satisfactory and no non-conformity related to cumulative air quality impact was observed. Nevertheless, in view of the public concern, the contractor was reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public. ET confirmed with the Resident Site Staff that the major construction activities under Contract HK/2009/02 around the concerned location conducted on 21 January 2015 include trenching grabbing for D-wall construction at temporary road eastward, shear pin installation at temporary road westward and ground Investigation drilling at temporary road westward	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Mitigation measures implemented by the Contractor of HK/2009/02 for the above construction works include regular water spraying at haul road, vehicle wheel-washing at the ingress/egress (Gate No. 4) to the temporary road, hard paving at the works area at temporary road northward and frequent water spraying at the ingress/egress (Gate No. 4) to the temporary road. According to the relevant site records, trenching grabbing for D-wall construction, shear pin installation and ground investigation drilling works were conducted at the concerned location. Dust mitigation measures including water spraying for haul road, vehicle wheel washing and hard paving for a section of works area nearby public road were implemented by the Contractor of HK/2009/02 near the concerned location on 21 January 2015. Follow-up investigation was conducted on 5 February 2015 during weekly environmental inspection, dust mitigation measures including water spraying for dusty haul road and major dust generation works and provision of wheel washing combine with cleaning of public road were confirmed in place and no dust related impact from the construction works was observed. The Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on 21 January 2015 was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants. Based on reviewing relevant impact monitoring data, elevated TSP were recorded at monitoring stations across Wan Chai West area to North Point area and a non-Project related exceedance was recorded at nearby monitoring station CMA4a (at SPCA) on 21 January 2015 due to ambient air pollutant.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					In addition, it was noted that a section of the works area at the concerned location was not provided with site hoarding. Based on further review on relevant records it was noted that the works area at concerned section was either hard paved or have to maintain adequate line of sight due to traffic safety consideration. The Contractor of HK/2009/02 was advised to inform EPD with respect to the site constraint and provide relevant updated meeting records on the arrangement for review. In view of the public concern, the contractor has committed to conduct additional cleaning of the concerned public road section once a week to minimize potential nuisance caused to nearby road users. The contractor was also reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.	
20150409	07 April 2015 09 April 2015	EPD complaint (Ref.:H05/RS/00008074-15 dated 9 April 2015) received by ET on 09 April 2015	Construction site exit near Expo Drive Central; Construction site gate V2 & gate V8	Construction dust was generated from lorries transporting out of the construction via site exit without wheel washing	A public complaint regarding construction dust impact referred by EPD was received by ET on 09 April 2015 (EPD Ref.:H05/RS/00008074-15 dated 9 April 2015). The complainant reported that: Construction dust was generated from lorries transporting out of the construction via site exit near Expo Drive Central without wheel washing at the morning of 7 April 2015. Lorries were also found transporting out of the construction site via gates V2 and V8 without wheel washing and causing dust nuisance at about 10:30 hours on 9 April 2015. ET confirmed with the Resident Site Staff that on 7 April 2015, major vehicle movements included oil tanker passing at Gate V2 at Expo Drive East and dump truck passing at Gate V8 at Expo Drive Central under Contract HK/2009/01.	Interim report submitted to EPD on 17 April 2015, EPD advised no comment on 30 April 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					2. On 9 April 2015, major vehicle movements include oil tanker, crane lorry and dump truck passing at at Gate V2 at Expo Drive East and dump truck at Gate V8 at Expo Drive Central under Contract HK/2009/01. Mitigation measures adopted by the Contractor of HK/2009/01 at the above locations include water hose was provided for wheel washing at Gate V2 and Gate V8, concrete paving at site exit, dump truck fitted with mechanic cover and cleaned before leaving construction site, regular street washing at Expo Drive Central. According to the relevant site records under Contract HK/2009/01, on 7 April 2015, major vehicle movements included oil tanker passing at Gate V2 at Expo Drive East and dump truck passing at Gate V8 at Expo Drive Central under Contract HK/2009/01 while on 9 April 2015 major vehicle movements include oil tanker, crane lorry and dump truck passing at at Gate V2 at Expo Drive East and dump truck at Gate V8 at Expo Drive Central under Contract HK/2009/01. At the above locations, mitigation measures including water hose for wheel washing at Gate V2 and Gate V8; concrete paving at site exit; dump truck fitted with mechanic cover and cleaned before leaving construction site and regular street washing at Expo Drive Central were generally adopted by the Contractor of HK/2009/01. In view of the public concern on the complaint date, the Contractor of HK/2009/01 was advised to conduct cleaning at the concerned site exit point and the section of public road adjoining the site exit to clear any residue grit and silt desposit to avoid further dust impact.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow up inspection was conducted on 16 April 2015 during weekly environmental inspection and mitigation measures including water spraying for dusty haul road and provision of wheel washing were in place. The construction site exit was observed clear from residue silt / grit at the concerned location. In view of the public concern, the contractor was advised to conduct training to the construction site workers to enhance the effectiveness of wheel washing and to ensure proper wheel washing is provided for dump truck and other vehicle prior to leaving the construction site to avoid generating any dust nuisance.	
20150409A	03 April 2015 to 07 April 2015	EPD complaint (Ref.:H05/RS/00007861-15 dated 9 April 2015) received by ET on 09 April 2015	Construction site at Convention Avenue near Renaissance Harbour View Hotel	Construction noise was emanated from the construction site at Convention Avenue near Renaissance Harbour View Hotel during the period of Easter Holiday	A public complaint regarding construction noise impact referred by EPD was received by ET on 09 April 2015 (EPD Ref.:H05/RS/00007861-15 dated 9 April 2015). The complainant reported that construction noise was emanated from the construction site at Convention Avenue near Renaissance Harbour View Hotel during the period of Easter Holiday, including April 3 at about 13:00 hours. ET confirmed with the Resident Site Staff that from 3 April 2015 to 7 April 2015, from 08:00 hours to 18:00 hours, and at about 13:00 hours on 3 April 2015 at area CWB Tunnel Stage 3, backfilling works was conducted under HK/2009/01. Either 1 no. of dump truck and 1. no. of excavator was operated on site at each given time during the concerned period. According to the relevant site records under Contract HK/2009/01, from across 08:00hrs to 18:00hrs during the period from 3 April 2015 to 7 April 2015, backfilling works was conducted under Contract HK/2009/01 at CWB Tunnel Stage 3. Either 1 no. of dump truck and 1 no. of excavator was operated on site at each given time during the	Interim report submitted to EPD on 17 April 2015, EPD advised no comment on 30 April 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					concerned period and the relevant Construction Noise Permit GW-RS0104-15 for the works was in place and the same construction activity was undertaken at around 13:00hrs on 3 April 2015. No other concurrent construction activity was undertaken at the concerned location during the concerned period under Contract HK/2009/01. The construction activity conducted under Contract HK/2009/01 during the concerned period was in compliance with the statutory requirement. Nevertheless, in view of the concern regarding the noise nuisance raised by the public at the concerned location, it is considered desirable for the Contractor of HK/2009/01 to review the truck unloading procedures of the specific construction task to minimize potential noise emanated during the course for work.	
20150415	13 April 2015	ICC complaint case (ICC Case Ref.: 2-885677297 dated 13 April 2015) received by ET on 15 April 2015	Construction Site at Causeway Bay Typhoon Bay Shelter	Unnecssary light nuisance from the construction site	A public complaint regarding visual impact received by the RSS was referred to the ET on 15 April 2015 (ICC Case Ref.: 2-885677297 dated 13 April 2015). The complainant reported that "I live in a building next to Gloucester Road in Causeway Bay. Recently, I am suffering from unnecessary light source from the construction site. The banners of the construction companies are always illuminated with very bright lights." ET confirmed with the Resident Site Staff that the concerned lighting for the banners was maintained under Contract HY/2010/08. The concerned lighting for the banners was maintained under Contract HY/2010/08 and the concerned lighting was subsequently switched off at all times since 13 April 2015 to alleviate the lighting nuisance caused to the surroundings.	Final Investigation report issued on 20 April 2015 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20150423	21 April 2015	EPD complaint case (EPD Case Ref: :H05/RS/00009456-15 dated 23 April 2015) received by ET on 23 April 2015	Road work at Fleming Road and Convention Avenue near Renaissance Harbour View Hotel	Construction noise emanated from the road work at Fleming Road and Convention Avenue near Renaissance Harbour View Hotel causing nuisance	A public complaint regarding construction noise impact referred by EPD was received by ET on 23 April 2015 (EPD Ref.:H05/RS/00009456-15 dated 23 April 2015). The complainant reported that construction noise emanated from the road work at Fleming Road and Convention Avenue near Renaissance Harbour View Hotel almost every night recently causing nuisance. ET confirmed with the Resident Site Staff that from 21:00hrs on 20 April 2015 to 06:00hrs on 21 April 2015 and from 21:00hrs on 21 April 2015 to 06:00hrs on 22 April 2015, cooling main connection works was undertaken by the Contractor of Contract HK/2009/01 at the concerned location. Total 1 no. of crane lorry and 1 no. of excavator were in operation. According to the relevant site records under Contract HK/2009/01, from 21:00hrs on 20 April 2015 to 06:00hrs on 21 April 2015 and from 21:00hrs on 21 April 2015 to 06:00hrs on 22 April 2015, cooling main connection works was undertaken by the Contractor of Contract HK/2009/01 at the concerned location. Total 1 no. of crane lorry and 1 no. of excavator were in operation during the concerned period and the relevant Construction Noise Permit GW-RS0269-15 was confirmed in place. The construction activity conducted under Contract HK/2009/01 during the concerned period was in compliance with the statutory requirement. In view of the potential noise nuisance, a notice to affected parties was issued by the Contractor of Contract HK/2009/01 to the nearby residents including Renaissance Harbour View Hotel on 17 April 2015. Besides, construction works undertaken by other parties at the concerned location was observed at the concerned period.	Final Investigation report issued on 18 May 2015 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20150601	29 May 2015	EPD complaint case (EPD Case Ref: :H05/RS/00013254-15 dated 1 June 2015) received by ET on 23 April 2015	Construction site gates V2 and V3 near Expo Drive Central	Vehicle with plate no. TG2426 was found leaving the construction site at gate V2 near Expo Drive Central without wheel-washed	A public complaint regarding construction dust impact referred by EPD was received by ET on 01 June 2015 (EPD Ref.:H05/RS/00013254-15 dated 1 June 2015). The complainant reported that vehicle with plate no. TG2426 was found leaving the construction site at gate V2 near Expo Drive Central without wheel-washed at about 10:33hrs on 29 May 2015. The complainant also alleged that water spraying at the gates V2 and V3 near Expo Drive Central was insufficient causing dust nuisance to the public. ET confirmed with the Resident Site Staff that on 29 May 2015, vehicle record indicated that concerned vehicle TG 2426 has entered and exited the construction site via gate V3. Mitigation measures adopted by the Contractor of HK/2009/01 at the above locations include, water hose was provided for wheel washing at Gate V2 and Gate V3. According to the relevant site records under Contract HK/2009/01, vehicle record indicated that concerned vehicle TG 2426 has entered and exited the construction site via gate V3 on 29 May 2015 under Contract HK/2009/01. As confirmed by WDII RSS, the concerned construction site Gate V2 and Gate V3 have been closed from 31 May 2015 and formed part of the construction site area. Follow up inspection was conducted on 3 June 2015 during weekly environmental inspection and mitigation measures including wheel washing were implemented at construction exit gates around the concerned location despite a vehicle was observed leaving the construction site via Gate V8 without wheel washing. The Contractor was immediately advised to review and strengthen the control measures for vehicle exits to ensure wheel washing are provided for exiting vehicles.	Interim report submitted to EPD on 08 June 2015, EPD advised no comment on 22 June 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					In view of the public concern and the site observation, the Contractor of HK/2009/01 has implemented enhanced site exit control measures using red string to alert drivers to stop their vehicles for cleaning before leaving the construction site and wheel washing facilities including water hose were implemented at Gate V1 and Gate V10 around the concerned location and the vehicle gate V8 was subsequently closed. In addition, removal of spoil arising from wheel washing around site exit location would be conducted by the Contractor of HK/2009/01 as appropriate to alleviate for potential dust impact at construction site exits.	
20150608	04 June 2015	EPD Ref.:H05/RS/0013843-15 dated 8 June 2015	A portion of construction site of Contract HK/2012/08 outside Fleet Arcade	Construction noise was generated from the construction site of Contract HK/2012/08 at location outside Fleet Arcade during restricted hours including Sundays and General Holidays.	A public complaint regarding construction noise impact referred by EPD was received by ET on 8 June 2015 (EPD Ref.:H05/RS/00013843-15 dated 8 June 2015). The complainant reported that construction noise was generated from the construction site of Contract HK/2012/08 at location outside Fleet Arcade during restricted hours including Sundays and General Holidays. ET confirmed with the Resident Site Staff that from 08:00hrs to 18:00hrs on 31 May 2015 (Sunday), construction work including steel welding was conducted under Contract HK/2012/08 at site portion zone A1 opposite to Fleet Arcade. Total one welding machine was in operation. According to the relevant site records under Contract HK/2012/08, from 08:00hrs to 18:00hrs on 31 May 2015 (Sunday), construction work including steel welding was conducted under Contract HK/2012/08 site portion zone A1 opposite to Fleet Arcade. Total one welding machine was in operation and the relevant Construction Noise Permit GW-RS0296-15 was confirmed in place. The construction activity conducted under Contract	Interim report submitted to EPD on 16 June 2015 and EPD advised no comment on 20 July 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					HK/2012/08 during the concerned period was in compliance with the statutory requirement. Ad-hoc inspection was conducted during weekly environmental inspection on 9 June 2015 and it was noted that Construction Noise Permits under Contract HK/2012/08 were posted at site entrance locations for public inspection. In view of the potential noise nuisance, the Contractor was reminded to upkeep the site control system for construction works carrying out at restricted hours and night time for Construction Noise Permit compliance. Besides, other construction sites at the concerned location were observed. Furthermore, a meeting was held on 15 June 2015 between the EPD, Contractor of HK/2012/08, WDII RSS team and the Environmental Team on the public concern and the Contractor of HK/2012/08 has committed to review the re-application for the Construction Noise Permits GW-RS0223-15 and GW-RS0296-15 on usage of PMEs at a portion of site area outside the Fleet Arcade during public holiday including Sundays to minimize for the potential noise nuisance to nearby public.	
150622	18 June 2015	EPD Ref.:H05/RS/0015054-15 dated 22 June 2015	A mooring location near shore and at location outside Wan Chai Sports Ground	Dark smoke and malodour emission was observed from a hopper barge moored near shore and other construction plants under operation from the reclamation construction site	A public complaint regarding dark smoke and malodour concern referred by EPD was received by ET on 22 June 2015 (EPD Ref.: H05/RS/00015054-15 dated 22 June 2015). The complainant reported that dark smoke and malodour emission was observed from a hopper barge moored near shore and other construction plants under operation from the reclamation construction site with Contract no. HK/2009/02 at location outside Wan Chai Sports Ground caused air pollution. The complainant alleged that the said situation had been observed for a prolonged period.	Interim report submitted to EPD on 29 June 2015 and EPD advised no comment on 20 July 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					ET confirmed with the Resident Site Staff that reinforced bar fixing and concreting work (on 17 June 2015 only) were conducted at Portion 2 from 15 June 2015 to 19 June 2015. Total 3 nos. of mobile crane were in operation. On 17 June 2015, one no. of concrete pump truck and two nos. of concrete mixer were in operation. Excavation and Lateral Support was conducted at Portions 3 & 4 from 15 June 2015 to 19 June 2015. Total 4 nos. of excavator, 2 nos. of truck and 2 nos. of crawler crane were in operation. In addition, on 15 June 2015, 17 June 2015 and 19 June 2015, 1 no. of derrick barge was moored near Portions 3 & 4 for transportation of the excavated material away from site. According to the relevant site records under Contract HK/2009/02, from 15 June 2015 to 19 June 2015, reinforced bar fixing and concreting work (on 17 June 2015 only) were conducted at Portion 2 and total 3 nos. of mobile crane, one no. of concrete pump truck (on 17 June 2015 only) and two nos. of concrete mixer (on 17 June 2015 only) were in operation; excavation and lateral support was conducted at Portions 3 & 4 and total 4 nos. of excavator, 2 nos. of truck and 2 nos. of crawler crane were in operation. Based on relevant site record, no hopper barge was moored under Contract HK/2009/02 around the concerned location while 1 no. of derrick barge was moored under Contract HK/2009/02 near Portions 3 & 4 for transportation of the excavated material from Portions 3 & 4 away from site on 15 June 2015, 17 June 2015 and 19 June 2015 respectively. Follow-up inspection was conducted during weekly environmental inspection on 25 June 2015, no dark smoke and malodour emission was observed from the PMEs operating on-site. A derrick barge was	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					observed moored near Portions 3 & 4 and excavated material was transferred to the derrick barge by the excavators on land without barge operation and no particular dark smoke and malodour emission was observed. Nevertheless, the Contractor was reminded to conduct regular checking on the condition of the derrick barge and other PMEs deployed on site to ensure only well maintained PMEs are used to avoid potential dark smoke and maldour emission affecting nearby public.	
150714	11 July 2015	ICC Complaint (Ref:#2-1149562777) referred by RSS was received by ET on 14 July 2015	A portion of site area adjacent to Hing Fat Street Site entrance	Direct discharge of muddy effluent into marine waters	A public complaint regarding direct discharge of muddy effluent referred by RSS was received by ET on 14 July 2015 (ICC Ref.: #2-1149562777). The complainant reported that: Muddy effluent was directly discharged into nearby marine waters by Chun Wo worker. Further information was received by ET from RSS on 23 July 2015 and the complaint date was clarified to be 11 July 2015 and the concerned vehicle registration number shall be JV 7319. ET confirmed with the Resident Site Staff that no construction works was undertaken by the Contractors HY/2009/19 and adjacent Central WanChai Bypass Project construction site at the concerned location on 11 July 2015. No construction works was undertaken by the Contractor of HY/2009/19 and adjacent Central WanChai Bypass Project construction site at the concerned location on 11 July 2015 and the concerned vehicle (License Plate JV 7319 labelled as Chun Wo) was confirmed not belonging to the Contractor of HY/2009/19. Follow-up inspection was conducted during weekly environmental inspection on 14 July 2015, no direct discharge connection was further observed on site.	Updated Final investigation report submitted on 27 July 2015.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					No construction works was undertaken by Central WanChai Bypass Project at the concerned location and no sump pit or works area under Central WanChai Bypass Project associated with potential muddy effluent discharge was identified. In addition, a construction area with excavated pit under WSD Contract 12/WSD/10 was noted at the concerned location behind the alleged vehicle responsible for direct discharge of muddy effluent. Based on the further review on the information received on 23 July 2015, the alleged direct discharge was observed originating from the works area under WSD Contract 12/WSD/10 and not related to the Central Wan Chai Bypass Project construction works.	
150723	20 July 2015	EPD Ref.:H05/RS/0018040-15 dated 23 July 2015	Ex-Wanchai Ferry Pier near 720 & 722 Bus stop	Malodour from marine sediment	A public complaint regarding malodour referred by EPD was received by ET on 23 July 2015 (EPD Ref.: H05/RS/00018040-15 dated 23 July 2015). The complainant reported that malodour from marine sediment was scented at ex-Wanchai ferry pier near route 720 & 722 bus stop. (Contract HK/2009/02). ET confirmed with the Resident Site Staff that Rockfill placing works was conducted by one derrick barge at the concerned location (WCR3) under Contract HK/2009/02 on 20 July 2015. No marine sediment was stored or placed on site at the concerned location under Contract HK/2009/02 on 20 July 2015. According to the relevant site records under Contract HK/2009/02, rockfill placing works was conducted by one derrick barge at WCR3 area on 20 July 2015 and no marine sediment was stored or placed on site at the concerned location on the concerned date.	Interim report submitted to EPD on 30 July 2015. EPD advised no comment on 17 August 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up inspection was conducted during weekly environmental inspection on 29 July 2015. No marine sediment was observed stored or placed at the concerned location while it was noted that a culvert outfall with potential odour concern is located adjacent to the concerned location. Nevertheless, the Contractor was reminded to review the handling procedures in case of any future marine sediment handling at the concerned location and to consider the implementation of mitigation measures as appropriate to minimize potential malodour impact to nearby public.	
150904	01 Sept 2015	EPD Ref.: H05/RS/0002 2241-15 dated 04 September 2015 received by ET on 4 September 2015	East of New WanChai Ferry Pier	Dropping of excavated material from land to sea during loading of material	A public complaint regarding dropping of excavated material from land to sea referred by EPD was received by ET on 04 September 2015 (EPD Ref.: H05/RS/00022241-15 dated 04 September 2015). The complainant reported that dropping of excavated materials from land to sea during loading of materials by excavator at the construction site to work boat. (Contract HK/2009/02) ET confirmed with the Resident Site Staff that transferring of C&D materials from land to hopper barge by excavator at seaside along CWB Tunnel Portions 3 and 4 was undertaken by Contract HK/2009/02 on 01 September 2015. Mitigation measure including providing tarpaulin sheet to cover the gap between seawall and the hopper barge to prevent dropping of material to the sea was implemented by the Contractor. According to the relevant site records under Contract HK/2009/02, transferring of C&D materials from land to hopper barge by excavator at seaside along CWB Tunnel Portions 3 and 4 was carried out on 01 September 2015 and mitigation measures including provision of tarpaulin sheet between	Interim report submitted to EPD on 14 September 2015. EPD advised no comment on 5 October 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					seawall and the hopper barge was implemented by the Contractor of HK/2009/02 on the concerned date. Follow-up inspection was conducted during weekly environmental inspection on 10 September 2015. Transferring of C&D materials from land to barge by excavator was observed at the concerned location and mitigation measures including provision of tarpaulin sheet between seawall and hopper barge and the material transfer works was generally in order. Nevertheless, the Contractor of HK/2009/02 was reminded to maintain the handling procedure for C&D materials transfer from land to hopper barge and regularly inspect the condition of the tarpaulin sheet provided to ensure the nearby water quality are not affected by the loading and unloading of material from land side to hopper barge. The Contractor was reminded to maintain the handling procedure for C&D materials transfer from land to hopper barge and regularly inspect the condition of the tarpaulin sheet provided to ensure the nearby water quality are not affected by the loading and unloading of material from land side to hopper barge.	
150904	02 Sept 2015	EPD Ref.: H04/RS/0002 2385-15 dated 04 September 2015 received by ET on 04 September 2015	Location outside Fleet Arcade	Construction noise was generated from the construction site of HK/2012/08 at location outside Fleet Arcade during night time on weekdays and daytime during General Holidays. The complainant also concerned construction dust and exhaust emission from derrick barges during	A public complaint regarding construction noise and dust and exhaust emission referred by EPD was received by ET on 04 September 2015 (EPD Ref.: H04/RS/00022385-15 dated 04 September 2015). The complainant reported that construction noise was generated from the construction site of HK/2012/08 at location outside Fleet Arcade during night time on weekdays and daytime during General Holidays. The complainant also concerned construction dust and exhaust emission from derrick barges during transporting C&D material at the site. (Contract HK/2012/08)	Interim report submitted to EPD on 14 September 2015. 2 nd interim report submitted to EPD on 17 Dec 2015



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				transporting C&D material at the site.	ET confirmed with the Resident Site Staff that from 0800 hrs to 1800 hrs on 30 August 2015, removal of scaffold and timber and installation of bulkhead was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one generator and one circular saw were in operation. From 1900hrs on 30 August 2015 to 0700 on 31 August 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 1900hrs on 31 August 2015 to 0700hrs on 01 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 1900hrs to 2115 hrs on 01 September 2015, unloading of soil was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one derrick barge was in operation. From 2300hrs on 01 September 2015 to 0700hrs on 02 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. One derrick barge was deployed for unloading of soil on 02 September 2015 during daytime under Contract HK/2012/08 at the concerned location. Based on the relevant site records, from 0800 hrs to 1800 hrs on 30 August 2015, removal of scaffold	3 rd interim report submitted to EPD on 31 Dec 2015



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					and timber and installation of bulkhead was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one generator and one circular saw were in operation and the relevant Construction Noise Permit GW-RS0296-15 for the concerned operation was confirmed in place. From 1900hrs on 30 August 2015 to 0700 on 31 August 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location and from 1900hrs on 31 August 2015 to 0700hrs on 01 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 1900hrs to 2115 hrs on 01 September 2015, unloading of soil was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one derrick barge was in operation and the Construction Noise Permit GW-RS0296-15 for the concerned operation was confirmed in place. From 2300hrs on 01 September 2015 to 0700hrs on 02 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. In view of the above, the construction activities conducted under Contract HK/2012/08 during the concerned period was in compliance with the statutory requirement.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					In addition, one derrick barge was deployed for unloading of soil on 02 September 2015 during daytime under Contract HK/2012/08 at the concerned location. Follow-up inspection was conducted during weekly environmental inspection on 08 September 2015 and no dark smoke emission was observed from the derrick barge moored outside the concerned location. Nevertheless, the Contractor of HK/2012/08 was reminded to conduct regular checking on the condition of the all derrick barges deployed on site to ensure only well maintained equipment are used to avoid potential dark smoke emission affecting nearby public and the Contractor of HK/2012/08 was reminded to upkeep the site control system for construction works carrying out at restricted hours and night time for Construction Noise Permit compliance. The Contractor was reminded to conduct regular checking on the condition of derrick barges deployed on site to ensure only well maintained equipments are used on site to avoid potential dark smoke emission affecting nearby public. The Contractor of HK/2012/08 was reminded to upkeep the site control system for construction works carrying out at restricted hours and night time for Construction Noise Permit compliance.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
151117	Not specified	EPD complaint received by ET on 17 November 2015	Causeway Bay Typhoon Shelter	Improper handling or bentonite and marine sediment generated from construction works and contaminated discharge from water treatment plant into Victoria Harbour	A public complaint regarding illegal disposal of construction waste referred by EPD was received by ET on 17 November 2015. The complainant reported that over 10,000 m3 of bentonite after usage for construction of diaphragm wall was disposed of at Victoria Harbour. The Contractor recently deployed mobile crane to transfer the bentonite from mud pit on to works barge. The bentonite was then mixed with soil and transported to the Public Fill. During the course, seepage of slurry through grab generated drop off to marine waters and the soil mixing generated dust impact to nearby yacht club, typhoon shelter and affect nearby public and boats. Disposal of dredged marine sediment was not carried out in accordance with the Management of Dredged/Excavated Sediment. Instead the marine sediment was covered by sand and soil and transported to the Public Fill. White or greyish effluent was discharged directly into Victoria Harbour marine waters from wastewater treatment plant on construction site. In response to the complaint concern, additional water quality monitoring from end November 2015 to mid January 2016 until the post-diaphragm wall construction activities and all bentonite silos and residue bentonite slurry at TS3 were completely removed had been undertaken by the Environmental Team and additional site inspections	Interim investigation report submitted to EPD on 24 November 2015. 2nd interim investigation report submitted to EPD on 17 December 2015. 3rd interim investigation report submitted to EPD on 31 December 2015. Final investigation report submitted on 5 February 2016.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					have been conducted by the ET and the investigation findings were included in the interim investigation reports separately submitted to the EPD. In addition, the ET and IEC have conducted checking on the waste disposal records and site construction records with the CWB RSS team to confirm the key construction activities during the concerned period and the quantities of inert C&D material disposed. Specific enhancement on site supervision was undertake by the CWB RSS team to ensure the properly handling of the remaining bentonite slurry in terms of the following: Depth of the bentonite slurry at the primary mixing pit (at south of TS3) was recorded by RSS team daily at regular intervals starting from 22nd December 2015 to record the changes in the level of slurry, particularly before end of works and at the start of works on the next day to confirm no significant change in bentonite slurry level during non-working hours until the complete removal of the mud pit. During the silo dismantling stage, the amount of residue bentonite cleared from the remaining silo were monitored on daily basis to record of the residue bentonite transferred for mixing and final disposal.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					The Environmental Team will continue to keep in view on the contractor environmental mitigation measures during the routine inspections, with specific attention at TS3 area on the effectiveness of Contractor's remediation measures and check the implementation of site measures in accordance with the EIA and EM&A Manual recommendations.	
ICC complaint case (ICC Ref: 2-159316569 4) dated 26 November 2015	26 No 2015	ICC complaint received by ET on 27 November 2015	Construction area outside City Garden Block 11	Noise nuisance due to windblown slapping of a metal onto adjacent barrier at night time	A public complaint regarding noise impact referred by RSS was received by ET on 27 November 2015 (ICC Case Ref.: 2-1593165694 dated 26 November 2015). The complainant reported that noise was emanated from the IECL construction site outside City Garden Block 11 due to the windblown slapping of a metal sheet onto adjacent barrier causing nuisance to nearby residents at night time. ET confirmed with the Resident Site Staff that the noise nuisance was caused by the windblown action of the corrugated metal sheet loosely affixed onto the temporary noise barrier panel above a concrete block footing fronting City Garden. The noise nuisance was caused by the windblown action of the corrugated metal sheet loosely affixed onto the temporary noise barrier panel above a concrete blocking footing fronting City Garden. The concerned corrugated metal sheet was removed by the Contractor of HY/2009/19 on 27 November 2015 to avoid further generation of noise nuisance.	Final investigation report to be issued on 01 December 2015.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					The Contractor was reminded to check and ensure metal sheetings and other material stored within the construction site are properly affixed to avoid potential noise nuisance due to windblown action.	
EPD complaint case (EPD Ref: H04/RS/00 028924-15 dated 04 December 2015	12 Novemb er 2015	EPD complaint received by ET on 04 December 2015	Two International Finance Centre at Finance Street, Central	Construction dust generated from construction site near Two International Finance Centre	A public complaint regarding construction dust impact referred by EPD was received by ET on 04 December 2015 (EPD Ref: H04/RS/00028924-15). The complainant reported that excessive construction dust was generated from the construction site near Two International Finance Centre at Finance Street, Central ET confirmed with the Resident Site Staff that bridge works and drains/ sewers construction at the concerned location was undertaken by Contract HY/2009/18 on 12 November 2015. A stockpile which would be reused for backfilling was stored at the concerned location by Contract HY/2009/18 on 12 November 2015. Mitigation measures implemented by the Contractor for the above construction works including covering of idled portion of stockpile and dampening of the exposed stockpile was implemented for the stockpile at the concerned location.	1st interim report submitted to EPD on 14 December 2015 2nd interim report subitted to EPD on 4 January 2016 EPD advised no comment on 07 January 2015 on the report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to relevant site records confirmed by RSS, bridge works and drains/ sewers construction at the concerned location was undertaken by Contractor of HY/2009/18 on 12 November 2015 and a stockpile which would be reused for backfilling was stored at the concerned location. Mitigation measures including covering of idled portion of stockpile and dampening of the exposed stockpile was implemented for the stockpile at the concerned location. In view of the public concern on potential dust impact at the concerned location, the Contractor of HY/2009/18 rearranged the works sequence and placed concrete blocks at the bridge retaining wall to allow for early commencement of backfilling on 19 November 2015 to minimize the size of the stockpile at an earlier stage. Additional water sprinklers were installed on 27 November 2015 to further enhance the dampening of the stockpile surface during excavation. Follow-up inspection was conducted during weekly environmental inspection on 10 December 2015 and mitigation measures including covering of stockpile stored at the concerned location was implemented while it was observed that stockpiles stored near Man Chiu Street was not properly covered. The Contractor of HY/2009/18 was advised to promptly provide covering to all idled stockpile stored on site and the Contractor was reminded to enhance the	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					watering during excavated material handling near the concerned location. Further follow up inspection was conducted on 17 December 2015 and mitigation measures including covering and watering for idle stockpile and material handling were implemented.	
ICC complaint case (ICC Case Ref: 2-1656689815 dated 14 December 2015	14 December 2015	EPD complaint received by ET on 04 December 2015	Construction area outside City Garden Block 10 and Block 11	Incessant noise emanating from the construction site of the Island East Corridor link that forms part of the Central Wanchai Bypass Project	A public complaint regarding noise impact referred by RSS was received by ET on 16 December 2015 (ICC Case Ref.: 2-1656689815 dated 14 December 2015). The complainant reported that: Incessant noise emanating from the construction site of the Island Eastern Corridor Link that forms part of the Central-Wanchai Bypass Project. Over the past couple of weeks, there have been loud mechanical pounding at the construction site over the reclaimed area between Blocks 10 and 11 of City Garden. As can be seen, machines have been breaking open the concrete paved on top of the reclaimed area. Work often starts well before 9am on weekdays and, barring a brief period of lull during lunch hours, would often continue unabated untill after 5pm. Although I note that certain noise reduction measures have been put into place (e.g. the erection of flimsy noise barriers around the work area), the noise created is still enormous, and this has become a significant nuisance for residents	Final report was issued on 23 December 2015 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					living in nearby blocks of our estate, especially children and the elderly who have to stay at home for longer hours. ET confirmed with the Resident Site Staff that concreting breaking works was carried out with one breaker on 7, 9, 11, 12 and 14 December 2015 and the breaking works at the concerned location were completed on 14 December 2015 morning. Noise mitigation measures including temporary noise barriers near the point of breaking and covering the breaker with acoustic mat were provided during the concerned concrete breaking works. According to information confirmed by RSS, concreting breaking works was carried out by one excavator mounted breaker on 7, 9, 11, 12 and 14 December 2015 and the concerned breaking works outside City Garden Block 10 and Block 11 was completed on 14 December 2015 morning. Noise mitigation measures including temporary noise barriers near the point of breaking and covering the breaker with acoustic mat were provided during the concerned concrete breaking works. Based on the further review on the record of the environmental inspection conducted on 09 December 2015, the Contractor of HY/2009/19 was reminded to temporary noise barrier provided for the pile cap demolition shall follow the the Environmental Permit EP-364/2009/D requirement.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow up inspection was conducted during weekly environmental inspection on 17 December 2015, the concerned breaking works opposite to City Garden Block 10 and Block 11 was observed completed while the Contractor was reminded that the remaining section of temporary noise barrier in accordance with the latest Environmental Permit EP-364/2009/D shall be completed on site as soon as possible. According to the information provided by RSS, the temporary noise barrier in accordance with the Environmental Permit requirement opposite to City Garden was substantially completed on 21 December 2015. In view of the public concern, the Contractor was suggested to consider to review the works duration at daytime and conduct other future breaking works around the concerned location intermittently to minimize the potential noise nuisance caused to the surroundings.	
EPD Ref.: H05/RS/00 000570-16 dated 14 January 2016	07 January 2016	EPD complaint received by ET on 14 January 2016	Lung King Street	Operation of powered mechanical equipment at the construction site near Lung King Street after 1900hrs.	A public complaint regarding construction noise referred by EPD was received by ET on 14 January 2016 (EPD Ref.: H05/RS/00000570-16 dated 14 January 2016). The complainant reported that there was operation of powered mechanical equipment at the construction site near Lung King Street after 1900hrs. (Contract HK/2012/08) ET confirmed with the Resident Site Staff that from 1900hrs to 2115hrs on 06 January 2016, shifting of equipment and socket H-pile casing was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one crawler crane was in operation.	Interim investigation report submitted to EPD on 22 January 2016. EPD advised on 17 February no comment on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to the relevant site records provided by RSS, shifting of equipment and socket H-pile casing was undertaken by the Contractor of HK/2012/08 at the concerned location from 1900hrs to 2115hrs on 06 January 2016. Total one crawler crane was in operation and the relevant Construction Noise Permit GW-RS0976-15 for the concerned operation was confirmed in place. Based on the above, the construction activities conducted under Contract HK/2012/08 on 06 January 2016 after 1900hrs was in compliance with the statutory requirement. Nevertheless, the Contractor was reminded to upkeep the site control system for construction works carried out during restricted hours and night time for Construction Noise Permit compliance in view of the nearby public concern.	
ICC complaint case (ICC Ref.: #2-1754682833 and ICC Ref: #2-1759629742	19 January 2016	EPD complaint received by ET on 19 January 2016	Hung Hing Road	Drainage at Hung Hing Road, Causeway Bay near the entrance of Cross Harbour Tunnel was blocked and sewage was overflowing from the sewer.	Two public complaints regarding the subject matter on blocked drainage were referred by RSS was received by ET on 19 January 2016 (ICC Ref.: #2-1754682833 and ICC Ref: #2-1759629742). The first complainant (ICC Ref.: #2-1754682833) on 11 January 2016 reported that the drainage at Hung Hing Road, Causeway Bay near the entrance of Cross Harbour Tunnel was blocked and sewage was overflowing from the sewer. The first complainant on 13 January 2016 enquired the status of follow-up, the complainant reported that the sewage overflow was severe and pose environmental hygiene concern to the	Final investigation report issued on 27 January 2016



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					surroundings. The first complainant on 14 January 2016 reported that the situation was not improved and would escalate the case if not addressed. The second complainant on 12 January 2016 (ICC Ref: #2-1759629742) reported that a foul sewer was found choking and foul water flows onto the carriageways. ET confirmed with the Resident Site Staff that no discharge point from the Contractor of HY/2009/15 is located within the concern portion of public drain (roadside gully) along Hung Hing Road. The observed yellow pipe extending from the roadside gully at Hung Hing Road into the site area under Contract HY/2009/15 was installed by the Contractor of HY/2009/15 to pump excessive sewage from the roadside gully on 11 January 2016. According to relevant site records and information provided by RSS, a steady flow of wastewater, noticeably sewer-like odour, was seeping through an existing sewage manhole at Hung Hing Road on 11 January 2016 and resulting in the formation of local ponding formed around the low point gully nearby. Based on relevant site information, no discharge point from the Contractor of HY/2009/15 was located at the concerned public drain (roadside gully) along Hung Hing Road while the observed yellow pipe extending from the roadside gully at Hung Hing Road into Contract HY/2009/15 site area was installed by the Contractor of HY/2009/15 to pump excessive sewage from the roadside gully on 11 January 2016. In view of no discharge point established under Contractor HY/2009/15 was observed at the concerned portion of Hung Hing Road, no direct information	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					indicating the association with the Contractor of HY/2009/15 is considered available. Follow up inspection was conducted during the weekly environmental inspection on 26 January 2016, no further accumulation of wastewater and no particular blockage of the concerned roadside gully at Hung Hing Road was observed. In addition, no overflow from the roadside sewer was observed. Nevertheless, the Contractor of HY/2009/15 was reminded to upkeep the site exit condition to avoid any potential impact to the surroundings.	
EPD complaint case (EPD Case Ref.:H05/RS/00001524-16	22 January 2016	EPD complaint received by ET on 22 January 2016	Hung Hing Road	Construction wastewater from the China Stat's construction site under Contract HY/2009/15 was discharged from the site exit at Hung Hing Road near the Royal Hong Kong Yacht Club to the carriage of Hung Hing Road causing accumulation of stagnant water	A public complaint regarding the blockage of public drainage referred by EPD was received by ET on 22 January 2016 (EPD Case Ref.: H05/RS/00001524-16). The complainant reported that construction wastewater from the China State's construction site under Contract HY/2009/15 was discharged from the site exit at Hung Hing Road near the Royal Hong Kong Yacht Club to the carriage of Hung Hing Road causing accumulation of stagnant water starting from 11 January 2016. ET confirmed with the Resident Site Staff that no construction activities with potential runoff at the main entrance of PRE Office was conducted under Contractor of HY/2009/15 on 11, 14, 15 and 17 January 2016. Concreting for Seawall Reinstatement at TPCWAE was conducted under Contractor of HY/2009/15 on 12 January 2016 and 18 January 2016. Concreting for construction works at covered Tunnel by using concrete pump at TPCWAE was conducted under Contractor of HY/2009/15 on 13 January 2016 and 16 January 2016. According to relevant site records and information	Interim investigation report submitted to EPD on 01 February 2016. EPD advised on 17 February no comment on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					provided by RSS, a steady flow of wastewater, noticeably sewer-like odour, was seeping through an existing sewage manhole at Hung Hing Road on 11 January 2016 and resulting in the formation of local ponding formed around the low point gully nearby. Based on relevant site information provided by RSS, no construction activity with potential runoff at the main entrance of PRE Office were conducted under Contractor of HY/2009/15 on 11, 14, 15 and 17 January 2016 while concreting for seawall reinstatement at TPCWAE were conducted on 12 January 2016 and 18 January 2016 and concreting for construction works at covered Tunnel by using concrete pump at TPCWAE were conducted on 13 January 2016 and 16 January 2016. All construction runoff was pumped to the wastewater treatment facility. In addition, no discharge point from the Contractor of HY/2009/15 was located at the concerned public drain (roadside gully) along Hung Hing Road. Follow up inspection was conducted during the weekly environmental inspection on 26 January 2016. No further accumulation of wastewater and particular blockage of the concerned roadside gully at Hung Hing Road was observed and no overflow from the roadside sewer was observed. The condition of the construction site exit under HY/2009/15 was generally in order and no particular construction surface runoff was observed. Nevertheless, the Contractor of HY/2009/15 was reminded to upkeep the site exit condition to avoid any potential impact to the surroundings.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref.: H05/RS/000 03169-16 dated 16 February 2016	16 February 2016	EPD complaint received by ET on 16 February 2016	West of HKCEC	Construction work at construction site of CEDD Wan Chai Development Phase II reclamation project around 2200hrs	A public complaint regarding construction works at restricted hours referred by EPD was received by ET on 16 February 2016 (EPD Ref.:H05/RS/00003169-16 dated 16 February 2016). The complainant reported that: There was construction work at construction site of CEDD Wan Chai Development Phase II reclamation project around 2200hrs on 06 February 2016 at the west of HKCEC within the work area of Contract HK/2012/08. ET confirmed with the Resident Site Staff that from 1900hrs to 2300hrs on 06 February 2016, no site activity was undertaken by the Contractor of HK/2012/08 at the concerned location and site activities under the Contractor of HK/2012/08 at the concerned area were stopped around 1700hrs on 06 February 2016. According to the relevant site records provided by RSS, from 1900hrs to 2300hrs on 06 February 2016, no site activity was undertaken by the Contractor of HK/2012/08 at the concerned location and site activities under the Contractor of HK/2012/08 at the concerned area were stopped around 1700hrs on 06 February 2016. Nevertheless, the Contractor was reminded to upkeep the site control system for any construction works carried out during restricted hours and night time for Construction Noise Permit compliance.	Interim investigation report submitted to EPD on 23 February 2016.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC Ref.: CASE#2-1938637403 dated 01 March 2016	01 March 2016	ICC complaint received by ET on 03 March 2016	Lung King Street near the parking spaces for motorcycles	Construction noise was emanated from road works	A public complaint regarding construction noise referred by ICC was received by ET on 03 March 2016 (ICC Ref.: CASE#2-1938637403 dated 01 March 2016). The complainant reported that construction noise was emanated from road works located between Lung Wo Road and Lung Wui Road Interface. Further information was referred by RSS on 15 March 2016, the complainant clarified on 15 March 2016 that construction noise was emanated from road works located between Lung Wo Road and Lung Wui Road Interface during midnight and has lasted for one and half month resulting in nuisance to nearby residence. Further information was referred by RSS on 18 March 2016, the complainant further clarified on 18 March 2016 that the concerned location shall be Lung King Street near the parking spaces for motorcycles and the Contract no. as stated on the publicity board is HK/2012/08. Furthermore, the complainant identified the noise was from power generators. ET confirmed with the Resident Site Staff that there was neither construction works nor operation of power generators under Contract HK/2012/08 at the concerned location from 1900hrs to 0700hrs during the period from 23 February 2016 to 14 March 2016. Based on the complaint information referred by ICC on 3 March 2016, according to the relevant site records provided by RSS, from 0800hrs to 1800hrs on both 29 February 2016 and 01 March 2016, drainage works was undertaken by Contract HK/2012/08 at Lung Wo Road and one excavator was in operation for soil excavation. Follow up inspection was conducted during the weekly environmental site inspection on 08 March 2016	1st investigation report issued on 11 March 2016. 2nd investigation report issued on 23 March 2016 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					and no particular noise emanating works was observed. Based on the further information provided by the complainant on 15 March 2016, the complainant clarified on 15 March 2016 that Construction noise was emanated from road works located between Lung Wo Road and Lung Wui Road Interface during midnight and has lasted for one and half month resulting in nuisance to nearby residence. On 18 March 2016, the complainant further clarified on 18 March 2016 that the concerned location shall be Lung King Street near the parking spaces for motorcycles and the Contract no. as stated on the publicity board is HK/2012/08. Furthermore, the complainant identified the noise was from power generators. According to the relevant site records provided by RSS, there was neither construction works nor operation of power generators under Contract HK/2012/08 at the concerned location from 1900hrs to 0700hrs during the period from 23 February 2016 to 14 March 2016. Nevertheless, in view of the public concern, the Contractor is recommended to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref.: H05/RS/000 05206-16 dated 10 March 2016	07 March 2016	EPD complaint received by ET on 10 March 2016	Waterfront at Lung King Street	Construction dust, plant exhaust and construction noise generated from the construction work of Contract HK/2012/08 at waterfront of Lung King Street caused nuisance, and the water quality at the waterfront of Lung King Street was becoming worse that accumulation of the floating refuse and foam was found	A public complaint regarding construction dust, plant exhaust, construction noise and water quality referred by EPD was received by ET on 10 March 2016 (EPD Ref.: H05/RS/00005206-16 dated 10 March 2016). The complainant reported that construction dust, plant exhaust and construction noise generated from the construction work of Contract HK/2012/08 at waterfront of Lung King Street caused nuisance, and the water quality at the waterfront of Lung King Street was becoming worse that accumulation of the floating refuse and foam was found. ET confirmed with the Resident Site Staff that soil excavation at ELS area, Zone A2(2), was carried out, where at approx. 100m from the waterfront of Lung King Street from 08:00 hrs to 18:00 hrs on 07 March 2016 under Contract HK/2012/08. Two excavators were involved at that location. Erection of falsework for culvert L was carried out near the waterfront of Lung King Street from 08:00 hrs to 18:00 hrs on 07 March 2016 under Contract HK/2012/08. One lorry crane was involved for lifting falsework elements. Dust suppression measures including the water sprinklers were installed along site haul road. Regularly removed the floating refuse at the waterfront of Lung King Street was conducted by the Contractor of HK/2012/08. The concerned observed floating foam at the waterfront of Lung King Street was found originating from the diverted cooling mains discharge. According to the relevant site records provided by RSS, soil excavation at ELS area, Zone A2(2) was carried out, where at approx.100m from the waterfront of Lung King Street under Contract	Interim investigation report submitted to EPD on 18 March 2016. EPD advised no comment on 29 April 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					HK/2012/08 from 08:00hrs to 18:00hrs on 07 March 2016 and two excavators were in operation at that location while erection of falsework for culvert L was carried out near the waterfront of Lung King Street from 08:00hrs and 18:00hrs on 07 March 2016 under Contract HK/2012/08 and one lorry crane was involved for lifting falsework elements. Dust suppression measures including the use of water sprinklers along the site haul road was implemented by the Contractor of HK/2012/08 and removal of floating refuse was regularly conducted at the waterfront of Lung King Street by the Contractor of HK/2012/08. Upon investigation, the concerned observed floating foam at the waterfront of Lung King Street was found originating from the diverted cooling mains discharge. Follow up inspection was conducted during the weekly environmental site inspection on 15 March 2016 and dust suppression measures including watering for haul road, tarpaulin sheet covering for cement bags stored on site and three side and top covering for grouting station were implemented while and no dark smoke emission from the plant and machinery deployed on site was observed. Noise mitigation measures including acoustic covering was implementing for excavator mounted breaker. In addition, removal of floating refuse on site was observed implemented by the Contractor of HK/2012/08 and no accumulation of floating refuse was found. The concerned foam originating from diverted cooling mains discharge was observed during inspection and the dispersion of the concerned foam of unknown chemical nature was observed isolated from the nearby public area. Nevertheless, in view of the public concern, the	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Contractor was recommended to maintain regular checking of the plants and equipment deployed on site to avoid potential air quality impact to the nearby public and to maintain adequate dust suppression measures on site to avoid potential dust impact to the surroundings. The Contractor was reminded to maintain regular cleaning of floating refuse within the construction site area to avoid potential nuisance to the surroundings. The Contractor was also reminded to maintain the noise mitigation measure if breaking works would be required. The Contractor was also suggested to reflect the observed foam to relevant Cooling Mains owners.	
EPD Ref.: H05/RS/000 06732-16 dated 10 March 2016	23 March 2016	EPD complaint received by ET on 31 March 2016	Seafront opposite to City Garden	Muddy water discharge from construction site outside City Garden	A public complaint regarding direct discharge of muddy effluent referred by EPD was received by ET on 31 March 2016 (Case Ref.: H08/RS/00006732-16). The complainant reported that: Muddy water was observed discharged from the construction site of Central – Wan Chai Bypass – Tunnel (North Point Section) and Island Eastern Corridor Link (Contract No. HY/2009/19) into Victoria Harbour via a drain hole. ET confirmed with the Resident Site Staff that pipe Laying works between Pier 32 and Pier 33 and excavation and blinding works for Manhole at Pier 34 were in progress on 22 March 2016. The observed drain hole was identified to be the outlet point of a manhole and a section of an abandoned U-channel (extending from the concerned manhole to the Hong Kong Electric Substation in length along the site boundary) was adjoining the concerned manhole and sandbag was previously placed at the U-channel at the location near the inlet point to the concerned manhole.	The interim investigation report was submitted to EPD on 11 April 2016. EPD advised no comment on 02 September 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Based on the site records confirmed by RSS, pipe laying works between Pier 32 and Pier 33 and excavation and blinding works for Manhole at Pier 34 were in progress on 22 March 2016. The observed drain hole was identified to be the outlet point of a manhole and a section of an abandoned U-channel (extending from the concerned manhole to the Hong Kong Electric Substation in length along the site boundary) was adjoining the concerned manhole and sandbag was previously placed at the U-channel at the location near the inlet point to the concerned manhole. In addition, no site discharge point was connected to the aforesaid U-channel and the concerned manhole. In view of the environmental concern, the following remedial and precautionary actions were taken by the Contractor of HY/2009/19 on 29 March 2016. i) Plugging the inlet point of the concerned manhole (connecting to the abandoned U-channel) with concrete; ii) Plugging the outlet of the concerned manhole (connecting to the observed drain hole) with concrete; iii) Filling the concerned manhole with rubbles; iv) Shifting the unused wastewater treatment plant around the concerned location to other site location for use. Follow-up inspection was conducted by the Environmental Team on 06 April 2016. No further contaminated runoff discharge was observed from the concerned drain hole and precautionary measures including provision of concrete bunding was implemented along the site boundary at the concerned location to avoid potential surface overflow. The pipe laying works and the excavation works was found at distant location	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					away from the concerned drain hole with no surface drain connection and no particular effluent was generated from the work. As such, no information indicate the discharge was related to the above construction activities. However, it was noted that another section of surface drainage channel within the construction site (perpendicular in direction to the initial identified abandoned U-channel) was also in connection to concerned manhole and minor residue mud deposition was observed within the surface drainage channel. Despite the above additional surface drainage channel identified, the outlet point of concerned final manhole (in connection with the observed drain hole) was observed plugged with concrete and filled with rubbles as rectification measure to avoid any further contaminated runoff discharge via the observed drain hole. Nevertheless, the Contractor of HY/2009/19 was reminded to conduct regular cleaning works for site surface drainage channel to avoid accumulation of silt and soil and avoid potential overflow by directing the surface runoff within the surface drainage channel to proper collection point for necessary treatment prior to discharge. The Contractor of HY/2009/19 was also reminded to check and review other surface drainage channel within the construction site to avoid potential runoff related impact via surface drainage channel to the nearby waters. In addition, it was noticed that water was discharged from a piping extending from City Garden and the discharged water would result in seepage across the site hoarding into the abandoned U-channel. The Contractor of HY/2009/19 was suggested to liaise with the City Garden Management Office for proper connection	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					of the observed pipping with discharge to prevent further seepage water into the construction site.	
H08/RS/000 07662-16	05 April 2016	EPD complaint received by ET on 05 April 2016	Construction area opposite to Harbour Heights	Construction dust emission arising from drilling activity	A public complaint regarding construction dust emission was referred by EPD was received by ET on 05 April 2016 (Case Ref.: H08/RS/00007662-16). The complainant reported that construction dust emission arising from drilling activity from the construction site of Central – Wan Chai Bypass – Tunnel (North Point Section) and Island Eastern Corridor Link (Contract No. HY/2009/19). ET confirmed with the Resident Site Staff that drilling holes for installation of starter bars was carried out under Contract HY/2009/19 at the vertical cut face of the existing IEC road slab on 05 April 2016 Based on the site records confirmed by RSS, drilling holes for installation of starter bars was carried out under Contract HY/2009/19 at the vertical cut face of the existing IEC road slab on 05 April 2016 and according to the photo information provided by the EPD, no dust suppression measures was implemented during the observed drilling works on 05 April 2016. According to Air Pollution Control Ordinance, for pneumatic or power-driven drilling, cutting and polishing, water or a dust suppression chemical shall be continuously sprayed on the surface where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation that causes dust emission is carried out, unless the process is accompanied by the operation of an effective dust extraction and filtering device.	The interim report was submitted to the EPD on 14 April 2016. EPD conducted follow up site visit on rectification measures on 21 April 2016. A inspection record form (Pink Form) was issued to the Contractor regarding the observed incident. EPD advised no comment on 02 September 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up inspection was conducted on 06 April 2016, rectification actions including the use of vacuum suction to extract dust generated during the concerned drilling works was observed implemented by the Contractor of HY/2009/19 for starter bars drilling works.	
ICC Case Ref.:2-2036525055 dated 27 March 2016	27 March 2016	ICC complaint case received by ET on 11 April 2016	Victoria Park Road Pedestrian Pathway	Toppling of tree	An ICC public complaint regarding landscape aspect was referred by RSS was received by ET on 11 April 2016 (Case Ref.:2-2036525055). The complainant reported that a tree (6 meters in height and 1.5 meters in diameter) was found toppled at 111 Victoria Park Road, near Lamp post 38632 and blocking the Pedestrian pathway on 27 March 2016. ET confirmed with the Resident Site Staff that the concerned tree was identified as T710 and no construction activity in the vicinity of tree T710 on 27 March 2016 and no construction works are required in or near its vicinity. Based on the site records confirmed by RSS, the concerned tree was identified as the retained tree T710 maintained under the Contract of HY/2010/08 and the concerned tree T710 was located outside the assessment area in the relevant Project EIA Report. No construction works are required in the vicinity of concerned tree T710 and no construction activity was conducted in the vicinity of tree T710 on 27 March 2016. Nevertheless, based on RSS information, recent tree monitoring report indicates an existing cavity at trunk and the concerned tree T710 has been recommended to be felled in the tree risk assessment Form 2. With respect to the observed incident of the toppling of the concerned tree T710, the	Investigation Report issued on 15 April 2016 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Contractor of HY/2010/08 was instructed by RSS to remove the broken trunk/ remains to avoid impact to the surroundings. The concerned tree T710 shall be compensated by the Contractor of HY/2010/08 in accordance with the Development Bureau Technical Circular (Works) No. 7/2015 and the detail on compensation would be further agreed with Victoria Park Management Office. Follow-up inspection was conducted on 13 April 2016, and the remaining parts of the concerned tree T710 was observed felled to avoid further impact to nearby public road.	
Not available	12 April 2016	A CEDD public complaint referred by RSS was received by ET on 13 April 2016	East of Star Ferry Piers	Muddy water was observed to disperse from Contract HK/2009/02 site area to Victoria Harbour occasionally as there was no silt curtain installed under the buoyancy floats. The location concerned was the East of Star Ferry Piers (Contract No. HK/2009/02).	A CEDD public complaint regarding muddy dispersion referred by RSS was received by ET on 13 April 2016. The complainant reported that muddy water was observed to disperse from Contract HK/2009/02 site area to Victoria Harbour occasionally as there was no silt curtain installed under the buoyancy floats. The location concerned was the East of Star Ferry Piers (Contract No. HK/2009/02). ET confirmed with the Resident Site Staff that no marine construction activities or land construction activities under Contract HK/2009/02 at the concerned location on 12 April 2016. Surface runoff control measures including provision of concrete bund at the concerned location was implemented by Contract HK/2009/02. No soil & silt deposition along the seawall at the concerned location on 12 April 2016. No discharge point located in the vicinity of the concerned location under Contract HK/2009/02. Silt curtain with buoyancy floats acting as anchor points was installed at Monitoring Station RW21-P789 for Water intakes.	Investigation report issued on 19 April 2016 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Based on the site records confirmed by RSS, no marine construction activities or land construction activities was carried out under Contract HK/2009/02 at the concerned location on 12 April 2016 and no soil and silt deposition was found along the seawall at the concerned location and precautionary measures for site runoff control including provision of concrete bund along boundary of site area near the waterfront around the concerned location was implemented by the Contractor HK/2009/02. In addition, no discharge point under Contract HK/2009/02 was located in the vicinity of the concerned location. Based on information confirmed by RSS, the buoyancy floats deployed at the concerned location are acting as the anchor points for the silt curtain deployed around the WQM Station RW21-P789 for the WSD and Cooling Water Intakes group. Follow-up inspection was conducted on 14 April 2016, no surface runoff from the construction site nor discharge of contaminated effluent was observed around the concerned location and precautionary measures including the provision of concrete bund at the concerned location was observed maintained by the Contractor of HK/2009/02 and the silt curtain deployed around the WQM station RW21-P789 was generally in order. In view of the public concern on the water quality, the Contractor of HK/2009/02 was reminded to maintain effective surface runoff protection and provide proper collection point of construction effluent around the concerned location to avoid potential surface runoff related impact.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref.: H05/RS/000 08367-16 dated 13 April 2016	13 April 2016	A public complaint referred by EPD was received by ET on 13 April 2016	Outside the Hong Kong Academy for Performing Arts	Muddy water discharge from construction site	A public complaint regarding muddy water discharge referred by EPD was received by ET on 13 April 2016 (EPD Ref.: H05/RS/00008367-16 dated 13 April 2016). The complainant reported that muddy water was discharged from the construction work of Contract HK/2012/08 to the sea outside the Hong Kong Academy for Performing Arts on 13 April 2016 morning. ET confirmed with the Resident Site Staff that internal transport of soil to the hopper barge for storage via landing barge was conducted by Contractor of HK/2012/08 during 0800 hours to 1000 hours on 13 April 2016 at the sea outside the concerned location and 3 nos. of dump trucks were deployed for the operation. Protection measure including provision of sandbag bunding along the side of the landing barge was implemented by the Contractor of HK/2012/08. According to the relevant site records provided by RSS, internal transport of soil to the hopper barge for storage via landing barge was conducted by Contractor of HK/2012/08 during 0800 hours to 1000 hours on 13 April 2016 at the sea outside the concerned location and 3 nos. of dump trucks were deployed for the operation. Protection measure including provision of sandbag bunding along the side of the landing barge was implemented by the Contractor of HK/2012/08. In addition, amber rainstorm warning signal was hoisted from 0630 hours to 1200 hours on 13 April 2016 and during the above time period, muddy water was observed from the upstream of culvert L outside the HK/2012/08 site. Follow up inspection was conducted on 19 April 2016, protection measures including provision of	Interim investigation report was submitted to the EPD on 21 April 2016. EPD advised no further comment on 06 June 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					sandbag bunding along the side of the landing barge was implemented and no mud or soil deposition was observed along the seawall and no discharge point was located within the temporary water channel connecting the Culvert L outfall location to the Victoria Harbour. In addition, piling works was observed at the north side of Zone A1 on 19 April 2016 and construction effluent collection from piling work via sedimentation tank to wastewater treatment facility was implemented and steel barrier was installed around the piling works area to mitigate against potential surface runoff related impact. Nevertheless, in view of the public concern, the Contractor was reminded to maintain adequate perimeter embankment protection along the seawall boundary and maintain proper construction effluent collection system to avoid potential runoff related impact to nearby waters.	
EPD Ref: H05/RS/000 12646-16 dated 27 May 2016	26 May 2016	A public complaint referred by EPD was received by ET on 27 May 2016	Construction Site near Wanchai Ferry Pier	Operation of generator around the clock	A EPD complaint regarding noise nuisance referred by RSS was received by ET on 27 May 2016 (EPD Ref: H05/RS/00012646-16 dated 27 May 2016). The complainant reported that a generator was operated round-the-clock in the Chun Wo- CRGL JV construction site near Wanchai Ferry Pier that cause noise nuisance. (Contract No. HK/2009/02). ET confirmed with the Resident Site Staff that a generator deployed under Contract HK/2009/02 near the covered walkway for Wanchai Ferry Pier at Portion 2 area and was operated from 1900hrs on 24 May 2016 to 0700hrs on 25 May 2016 and from 1900hrs on 25 May 2016 to 0700hrs on 26 May 2016. The generator was used for the power supply of lighting inside Tunnel Portions 1 and 2. According to the relevant site records provided by	Interim investigation report submitted to EPD on 7 June 2016. EPD advised no further comment on 05 August 2016 on the report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					RSS, a generator deployed under Contract HK/2009/02 near the covered walkway for Wanchai Ferry Pier at Portion 2 area and was operated from 1900hrs on 24 May 2016 to 0700hrs on 25 May 2016 and from 1900hrs on 25 May 2016 to 0700hrs on 26 May 2016. The generator was used for the power supply of lighting inside Tunnel Portions 1 and 2. Based on review on site information, relevant Construction Noise Permits GW-RS0516-16 and GW-RS0390-16 for the operation of the concerned generator were confirmed in place while no sufficient site information was considered available to demonstrate the use of acoustic enclosure for the operation of the generator following the special condition 3d item 4. Despite the above, the Contractor of HK/2009/02 has suspended the use of the generator at the concerned location after 2300hours to minimize potential noise concern to the surroundings from 28 May 2016. Nevertheless, the Contractor of HK/2009/02 was reminded to upkeep the site control system for construction works carried out during restricted hours and night time for Construction Noise Permit compliance and maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref: H08/RS/000 14627-16 dated 16 June 2016	15 June 2016	A public complaint referred by EPD was received by ET on 16 June 2016	Construction area of Island Eastern Corridor near Sea View Estate.	Splashing from the working area of Island Eastern Corridor near Sea View Estate.	A public complaint was referred by EPD was received by ET on 16 June 2016 (Case Ref.: H08/RS/00014627-16). The complainant reported that his or her properties were covered by many water stains which were splashing from the working area of Island Eastern Corridor near Sea View Estate. ET confirmed with the Resident Site Staff that rebar fixing was carried out on 13 and 14 June 2016 under the Contractor of HY/2009/19 while formwork cleaning and laying concrete for stitching and curing work for concrete were carried out under the Contractor of HY/2009/19 on 15 June 2016 and 16 June 2016 respectively. Mitigation measures including provision of metal cover underneath the bridge deck in slanting position at Watson Road to prevent spilling of water onto public road and provision of tarpaulin sheet along the guard rails of the bridge deck at Pier 19-20 (opposite to Sea View Estate) to prevent splashing of water to outside area were implemented by the Contractor of HY/2009/19. Based on the site records confirmed by RSS, rebar fixing was carried out on 13 and 14 June 2016 under the Contractor of HY/2009/19 while formwork cleaning and laying concrete for stitching and curing work for concrete were carried out under the Contractor of HY/2009/19 on 15 June 2016 and 16 June 2016 respectively. Mitigation measures including provision of metal cover underneath the bridge deck in slanting position at Watson Road to prevent spilling of water onto public road and provision of tarpaulin sheet along the guard rails of the bridge deck at Pier 19-20 (opposite to Sea View Estate) to prevent splashing of water to outside area were implemented by the Contractor of HY/2009/19.	The interim report submitted to the EPD on 29 June 2016. EPD advised no comment on the interim report submitted and case closed on 02 September 2016.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow up inspection was conducted on 22 June 2016, mitigation measures including the use of metal cover underneath the bridge deck at Watson Road and provision of tarpaulin sheet along the guard rails of the section of bridge deck opposite to Sea View Estate were implemented by the Contractor of HY/2009/19. No particular spilling or splashing of construction water was observed during inspection around the concerned location. Nevertheless, in view of the public concern, the Contractor of HY/2009/19 was suggested that the direction of the water hose shall be pointed away from the public area as far as practicable during water use or watering for dust suppression to avoid potential splashing nuisance caused to the surroundings. The Contractor of HY/2009/19 was also reminded to maintain proper site drainage to direct surface runoff generated from construction works or cleaning to the proper collection point within site area to avoid potential nuisance to the surroundings.	
EPD Ref: H08/RS/000 16213-16 dated 14 July 2016	30 June 2016	A public complaint referred by EPD was received by ET on 14 July 2016	Construction Site of TS3 near Slip Road 8	Night time construction noise from construction works between 0200hrs to 0300hrs and construction dust emission from construction site of TS3 near Slip Road 8 section.	A public complaint referred by EPD was received by ET on 14 July 2016 (Case Ref.: H08/RS/00016213-16). The complainant reported the concern about night time construction noise from construction works between 0200hrs to 0300hrs and construction dust emission from construction site of TS3 near Slip Road 8 section. ET confirmed with the Resident Site Staff that excavation at TS3 and loading of material onto derrick barge (Shun Tat 28) by crawler crane was undertaken by the Contractor of HY/2010/08 from 19:00hrs to around 02:00hrs on 30 June 2016. Total one crawler crane was in operation. Noise mitigation measures including equipping the crawler crane with noise barrier was implemented	The interim report submitted to the EPD on 22 July 2016



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					by the Contractor of HY/2010/08. Dust mitigation measures including manual spraying of water and mist nozzles are deployed on the ground level and at the cofferdam. Based on the site records confirmed by RSS, excavation at TS3 and loading of material onto derrick barge (Shun Tat 28) by crawler crane was undertaken by the Contractor of HY/2010/08 from 19:00hrs on 29 June 2016 to around 02:00hrs on 30 June 2016. No construction works was conducted at the concerned location after around 02:00hrs on 30 June 2016. Total one crawler crane was in operation and noise mitigation measures including equipping the crawler crane with noise barrier was implemented by the Contractor of HY/2010/08. Based on review on relevant record, Construction Noise Permit GW-RS0434-16 for the operation of crawler crane at the concerned location was in place. However, based on relevant site record, it was noted that the crawler crane deployed during the concerned period could not match with the specific PME requirement under condition 3a (Crane, crawler, mounted with noise barrier (Kobelco 7250S)) of the Construction Noise Permit GW-RS0434-16 between 23:00hrs to 07:00hrs on the following day. Dust mitigation measures including manual spraying of water and mist nozzles were deployed on the ground level and at the cofferdam. Follow up inspection was conducted on 20 July 2016, the potential concerned excavation works at the concerned location was not observed and no particular dust impact was observed around the concerned location. In view of the above, the Contractor of HY/2010/08 was advised to review the site control system for	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					construction works carried out during restricted hours to check and ensure the model/ specific PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public. Also, the Contractor of HY/2010/08 was reminded to maintain sufficient watering for excavated material handling to avoid potential dust nuisance to the surroundings.	
EPD Ref: H08/RS/000 22448-16 dated 06 September 2016	04 Sept 2016	A public complaint referred by EPD was received by ET on 06 September 2016	Road construction works area near Causeway Bay Typhoon Shelter	Construction noise from road construction work near Causeway Bay Typhoon Shelter	A public complaint referred by EPD was received by ET on 06 September 2016 (Case Ref.: H08/RS/00022448-16). The complainant reported that construction noise from the road construction work near Causeway Bay Typhoon Shelter during 0800hrs to 2100 hrs on 04 September 2016 (Sunday) caused nuisance. The complainant also indicated that the construction noise was generated up to 0100 hrs on normal weekdays. ET confirmed with the Resident Site Staff that underwater welding of lagging plate at Zone C was conducted from 0800hrs to 2100hrs on 04 September 2016. Total 1 no. of generator and 1 no. of welding machine were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 01 September 2016 to 0100hrs on 02 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 02 September 2016 to 0100hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound	The interim report submitted to EPD on 20 September 2016. EPD advised no comment on 31 October 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					slow lane was conducted from 2300hrs to 2359hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Based on the site records confirmed by RSS, underwater welding of lagging plate at Zone C was conducted from 0800hrs to 2100hrs on 04 September 2016, total 1 no. of generator and 1 no. of welding machine were in operation and relevant Construction Noise Permit GW-RS0442-16 was in place. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 01 September 2016 to 0100hrs on 02 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 02 September 2016 to 0100hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs to 2359hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Relevant Construction Noise Permit GW-RS0531-16 was in place for the above construction activities. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref: H08/RS/000 24768-16 dated 07 October 2016	28 Sept 2016 04 Oct 2016	A public complaint referred by EPD was received by ET on 07 October 2016	Causeway Bay Typhoon Shelter	Construction work at the construction site in Causeway Bay Typhoon Shelter area was found after 1900hrs on 28 September 2016 and 04 October 2016 that caused noise nuisance.	A public complaint referred by EPD was received by ET on 07 October 2016 (Case Ref.: H08/RS/00024768-16). The complainant reported that construction work at the construction site in Causeway Bay Typhoon Shelter area was found after 1900hrs on 28 September 2016 and 04 October 2016 that caused noise nuisance. The complainant also reported that there were 5 concrete lorry mixers operating at the above site after 1900hrs on 04 October 2016. ET confirmed with the Resident Site Staff that concreting for tunnel structure in TS3 (W) was conducted from 1900hrs to 2300hrs on 28 September 2016. One concrete pump and two concrete lorry mixers were in operation. One no. of concrete lorry mixer was located at the East of TS3 (W) and one no. of concrete lorry mixer was located at the west of TS3 (W). Concreting for tunnel structure in TS3 (W) was conducted from 1900hrs to 2300hrs on 04 October 2016. One concrete pump and two concrete lorry mixers were in operation. One no. of concrete lorry mixer was located at the East of TS3 (W) and one no. of concrete lorry mixer was located at the west of TS3 (W). Based on the site records confirmed by RSS, concreting for tunnel structure in TS3 (W) was conducted from 1900hrs to 2300hrs on 28 September 2016 and from 1900hrs to 2300hrs on 04 October 2016 and total one concrete pump and two concrete lorry mixers were in operation during the above concerned periods. One no. of concrete lorry mixer was located at the East of TS3 (W) and one no. of concrete lorry mixer was located at the west of TS3(W) during the above concerned periods and relevant Construction Noise Permit	The interim investigation report was submitted to EPD on 18 October 2016.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					GW-RS0434-16 and GW-RS0407-16 were in place for the construction works conducted during the above concerned periods. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
EPD Ref: H05/RS/0002 9722-16 dated 22 November 2016	15 Nov 2016	A public complaint referred by EPD received by ET on 22 November 2016	Construction Site near Wanchai Ferry Pier	Noise was emanated in the Chun Wo – CRGLJV construction site near Wanchai Ferry Pier till late night and caused nuisance to nearby sensitive receivers.	An EPD complaint regarding noise nuisance referred by EPD was received by ET on 22 November 2016 (EPD Ref: H05/RS/00029722-16 dated 22 November 2016). The complainant reported that noise was emanated in the Chun Wo – CRGLJV construction site near Wanchai Ferry Pier till late night and caused nuisance to nearby sensitive receivers. ET confirmed with the Resident Site Staff that Excavation works at Portion 5 was conducted under Contract HK/2009/02 at Portion 5 area (West of Wan Chai Ferry Pier) from 1900hrs to 2300hrs on 14 November 2016. Total two crawler cranes, two excavators and two generators were operated at ground level and four excavators were operated below ground level. No construction activity was conducted under Contract HK/2009/02 from 2300hrs on 14 November 2016 to 0700hrs on 15 November 2016. Total two generators were operated at ground level for lighting illumination of Portion 5.	Interim investigation report submitted to EPD on 29 November 2016.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to information provided by RSS, excavation works at Portion 5 was conducted under Contract HK/2009/02 at Portion 5 area (West of Wan Chai Ferry Pier) from 1900hrs to 2300hrs on 14 November 2016. Total two crawler cranes and two excavators were operated at ground level and four excavators were operated below ground level. Two generators were operated at ground level. Based on review on site information, relevant Construction Noise Permits GW-RS0593-15 for the above construction activities and above operation of the generators were confirmed in place. No construction activity was conducted under Contract HK/2009/02 from 2300hrs on 14 November 2016 to 0700hrs on 15 November 2016 and two generators were operated at ground level for lighting illumination of Portion 5. In view of the public concern, the Contractor of HK/2009/02 confirmed that the two generators for lighting power supply at ground level after 2300hrs had been suspended and replaced by other two generators located below ground level at Portion 5 area since 23 November 2016 to minimize the noise impact to the surroundings. In addition, the Contractor of HK/2009/02 was reminded to upkeep the site control system for construction works carried out during restricted hours and night time for Construction Noise Permit compliance and maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public. Also, the Contractor of HK/2009/02 was recommended to review the enhancement noise mitigation measure to be adopted for the generators deployed at ground level before 2300hrs to alleviate potential noise concern to the surroundings.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD ref: H08/RS/0003 0890-16 dated 07 December 2016	24 Nov 2016	A public complaint referred by EPD received by ET on 07 December 2016	Construction Site at Victoria Park	Noise emanated from the construction site at Victoria Park after 1900hrs.	A public complaint referred by EPD was received by ET on 07 December 2016 (Case Ref.: H08/RS/00030890-16). The complainant reported that Noise was emanated in the construction site near Victoria Park after 19:00 and caused nuisance to nearby sensitive receivers on 24 November 2016. ET confirmed with the Resident Site Staff that welding works for the tie-rod for the vertical blinding concrete was undertaken by the Contractor of HY/2010/08 at the construction site in the Victoria Park from 1900hrs to 2300hrs on 24 November 2016. Total 3 nos. of welding machines (electric), 3 nos. of water pumps (electric) and 1 no. of AquaSED were in operation. Based on the site records confirmed by RSS, welding works for the tie-rod for the vertical blinding concrete was undertaken by the Contractor of HY/2010/08 at the construction site in the Victoria Park from 1900hrs to 2300hrs on 24 November 2016. Total 3 nos. of welding machines (electric), 3 nos. of water pumps (electric) and 1 no. of AquaSED were in operation and relevant Construction Noise Permit GW-RS0930-16 was in place for the construction works conducted during the above concerned period. In addition, according to relevant site information confirmed by RSS, the welding machines, water pumps and AquaSED were connected to and powered by Hong Kong Electric power grid. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	Investigation report submitted to EPD on 16 December 2016. Under EPD review



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD complaint H08/RS/000 01175-17 dated 16 January 2016	10 January 2017	A public complaint referred by EPD received by ET on 16 January 2017	Causeway Bay Typhoon Shelter	Construction work at the reclamation site in Causeway Bay Typhoon Shelter area (Under the Island Eastern Corridor) was found after 1900hrs on 10 January 2017 and the concrete lorry mixer and concrete pump may not comply with the Construction Noise Permit	A public complaint referred by EPD was received by ET on 16 January 2017 (Case Ref.: H08/RS/00001175-17). The complainant reported that construction work at the reclamation site in Causeway Bay Typhoon Shelter area (Under the Island Eastern Corridor) was found after 1900hrs on 10 January 2017. The complainant reported that there were 3 concrete pumps and around 10 concrete lorry mixers operating at the above site during the said period which may not comply with the Construction Noise Permit. ET confirmed with the Resident Site Staff that concreting of tunnel structure was conducted under Contract HY/2010/08 at Temporary Reclamation Area TS3 between 1900hrs and 2000hrs on 10 January 2017. Total 3 nos. of Lorry Mounted Concrete Pumps and 6 nos. of Concrete Lorry Mixers were operated at TS3 while temporary noise barrier was provided for 2 nos. of the operating Lorry Mounted Concrete Pumps and 4 nos. of the operating Concrete Lorry Mixers. Total 1 no. of Concrete Lorry Mixer was at stand-by within TS3 Works area. Concreting of tunnel structure was conducted under Contract HY/2010/08 at Temporary Reclamation Area TS3 between 2000hrs and 2030hrs 10 January 2017. Total 2 nos. of Lorry Mounted Concrete Pump and 4 nos. of Concrete Lorry Mixers were operated at TS3 while temporary noise barrier was provided for 1 no. of the operating Lorry Mounted Concrete Pumps and 2 nos. of the operating Concrete Lorry Mixers. Total 1 no. of Concrete Lorry Mixer was at stand-by within TS3 Works area.	Interim investigation report submitted to EPD on 03 February 2017.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Concreting of tunnel structure was conducted under Contract HY/2010/08 at Temporary Reclamation Area TS3 between 2030hrs and 2300hrs 10 January 2017. Total 1 no. of Lorry Mounted Concrete Pump and 2 nos. of Concrete Lorry Mixers were operated at TS3. Based on the site records confirmed by RSS, concreting of tunnel structure was conducted under Contract HY/2010/08 at Temporary Reclamation Area TS3 between 1900hrs and 2300hrs on 10 January 2017. From 1900hrs to 2000hrs, total 3 nos. of Lorry Mounted Concrete Pumps and 6 nos. of Concrete Lorry Mixers while temporary noise barrier was provided for 2 nos. of the operating Lorry Mounted Concrete Pumps and 4 nos. of the operating Concrete Lorry Mixers. Total 1 no. of Concrete Lorry Mixer was at stand-by within TS3 Works area. From 2000hrs to 2030hrs, total 2 nos. of Lorry Mounted Concrete Pump and 4 nos. of Concrete Lorry Mixers were operated at TS3 while temporary noise barrier was provided for 1 no. of the operating Lorry Mounted Concrete Pumps and 2 nos. of the operating Concrete Lorry Mixers. Total 1 no. of Concrete Lorry Mixer was at stand-by within TS3 Works area. From 2030hrs to 2300hrs, total 1 no. of Lorry Mounted Concrete Pump and 2 nos. of Concrete Lorry Mixers were operated at TS3. Relevant Construction Noise Permit GW-RS1232-16 (Corresponding PME Groups operated include Group M, Group K and Group H) was in place for the construction works conducted during the above concerned periods and based on RSS information, a designated personnel on-site was responsible for controlling and supervising the switching between PME Groups. Meanwhile, there	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					is no sufficient information to conclude if the concerned PME(s) (Concrete Lorry Mixer and Lorry Mounted Concrete Pump) deployed behind the temporary noise barrier provided were not visible to nearby sensitive receivers. As multiple PME grouping under the Construction Noise Permit are involved, the Contractor of HY/2010/08 was reminded to strictly follow the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in strict compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
ICC complaint case (Ref: #2-3218844776) dated 23 December 2017	22 Dec 2016	ICC complaint case referred by RSS received by ET on 18 January 2017	Construction Site Gate Exit near Expo Drive East	No wheel washing from CEDD work site, no supervision from the Resident Site Staff, mud was dispersed on the road and flush to the communal drain by Chun Wo-China Railway JV HK/2009/02.	A public complaint regarding the subject matter on wheel washing referred by RSS was received by ET on 18 January 2017 (ICC Ref: #2-3218844776). The complainant reported that no wheel washing from CEDD work site, no supervision from the Resident Site Staff, mud was dispersed on the road and flush to the communal drain by Chun Wo-China Railway JV HK/2009/02. ET confirmed with the Resident Site Staff that the concerned location was Site Exit Gate No. 6 at Expo Drive East operated and maintained under HK/2009/02 on 22 December 2016. Site measures including provision of wheel washing facility was implemented by the Contractor of HK/2009/02 on the concerned date. According to information provided by RSS, the concerned location was Site Exit Gate No. 6 at Expo Drive East operated and maintained under HK/2009/02 on 22 December 2016. In view of the environmental concern, remedial measures including i) instructing all workers to conduct wheel	Final investigation report issued on 23 January 2017.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					washing within the designated location with collection pit to prevent overflow of washing effluent and ii) manual removal of dirt/silt by worker instead of water flushing in case of dirt/muddy trail found on road were implemented by the Contractor on 28 December 2016. Also, the Contractor of HK/2009/02 was further reminded by the WDII RSS to maintain proper wheel washing facilities at Gate No.6 and inspect regularly to ensure that all vehicles leaving the site to public roads are free of mud. Nevertheless, the Environmental Team further reminded the Contractor on 04 January 2017 that site measures including i) wheel washing operation shall be conducted at the designated location behind the backfall to avoid overflow of washing effluent onto public road ii) any silt/ soil deposited of the public road shall be cleared manually shall be strictly followed and relevant remedial actions were taken by the Contractor of HK/2009/02 on 04 January 2017. According to site inspection conducted on 17 January 2017, the concerned site exit Gate No.6 was maintained in proper condition, no silt/ mud deposition was observed on the public road and wheel washing was conducted by the Contractor of HK/2009/02 at the designated location within the construction site to avoid overflow of washing effluent onto nearby public road.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC complaint case (Ref: #2-351203393 6) dated 20 February 2017	20 February 2017	ICC complaint case referred by RSS received by ET on 24 February 2017	Victoria Park Swimming Pool	Noise was emanated from the construction site near Victoria Park Swimming Pool between 2300hrs to 2400hrs in the past months and caused nuisance.	An ICC complaint referred by RSS was received by ET on 24 February 2017 (CASE#2-3512033936). The complainant reported that noise was emanated from the construction site near Victoria Park Swimming Pool between 2300hrs to 2400hrs in the past months and caused nuisance. ET confirmed with the Resident Site Staff that no works was conducted under Contract HY/2010/08 near Victoria Park Swimming Pool (Hing Fat Street) during the restricted hours (from 1900hrs to 0700hrs on the following day) from 21 December 2016 to 20 February 2017. No works was conducted under Contract HY/2010/08 near Victoria Park Swimming Pool (Hing Fat Street) during the restricted hours (from 1900hrs to 0700hrs on the following day) from 21 December 2016 to 20 February 2017. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	Final Investigation Report issued on 02 March 2017 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC complaint case (Ref: #2-3515474831) dated 21 February 2017	21 February 2017	ICC complaint case referred by RSS received by ET on 24 February 2017	Construction Site near Victoria Park Swimming Park and Causeway Bay Typhoon Shelter	Noise was emanated from the construction site near Victoria Park Swimming Pool between 2300hrs to 2400hrs in the past months and caused nuisance.	An ICC complaint referred by RSS was received by ET on 24 February 2017 (CASE#2-3515474831). The complainant reported that noise was emanated from the construction site near Victoria Park Swimming Pool and Causeway Bay Typhoon Shelter between 1900hrs to 2400hrs in the past months and caused nuisance. ET confirmed with the Resident Site Staff that concreting of tunnel structure at Temporary Reclamation Area TS3 were conducted under Contract HY/2010/08 between 1900hrs and 2300hrs on 13, 14, 15, 16 and 18 February 2017. Total 3 nos. of concrete pump and 6 nos. of concrete lorry mixers were operated. Concreting of tunnel structure at Temporary Reclamation Area TS3 were conducted under Contract HY/2010/08 between 1900hrs and 2100hrs on 21 February 2017. Total 3 nos. of concrete pump and 6 nos. of concrete lorry mixers were operated. Concreting of tunnel structure at Zone C was conducted under Contract HY/2010/08 between 1900hrs to 2300hrs on 17 and 20 February 2017. Total 1 no. of concrete pump and 2 nos. of concrete mixers were operated. Bar bending at Zone C was conducted under Contract HY/2010/08 between 1900hrs to 2300hrs on 13, 14, 15, 16, 18 and 19 February 2017. Total 1 no. bar bender and cutter was operated. No works was conducted under Contract HY/2010/08 near Victoria Park Swimming Pool (Hing Fat Street) during the restricted hours (from 1900hrs to 0700hrs on the following day) across the period from 13 February 2017 to 21 February 2017. Based on the site records confirmed by RSS, no works was conducted under Contract HY/2010/08	Final Investigation Report issued on 07 March 2017 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					near Victoria Park Swimming Pool (Hing Fat Street) during the restricted hours (from 1900hrs to 0700hrs on the following day) from 13 February 2017 to 20 February 2017. Concreting of tunnel structure at Temporary Reclamation Area TS3 was conducted under Contract HY/2010/08 between 1900hrs and 2300hrs on 13, 14, 15, 16 and 18 February 2017 and total 3 nos. of concrete pumps and 6 nos. of concrete lorry mixers were operated. Concreting of tunnel structure at Temporary Reclamation Area TS3 were conducted under Contract HY/2010/08 between 1900hrs and 2100hrs on 21 February 2017 and total 3 nos. of concrete pump and 6 nos. of concrete lorry mixers were operated. Relevant Construction Noise Permit GW-RS0029-17 was in place while it is considered that there is no sufficient information to indicate whether the Powered Mechanical Equipment were deployed at the designed location stipulated under the relevant Construction Noise Permit with noise mitigation measures required. Concreting of tunnel structure at Zone C was conducted under Contract HY/2010/08 between 1900hrs to 2300hrs on 17 and 20 February 2017. Total 1 no. of concrete pump and 2 nos. concrete mixers were operated. Bar bending at Zone C was conducted under Contract HY/2010/08 between 1900hrs to 2300hrs on 13, 14, 15, 16, 18 and 19 February 2017 and total 1 no. bar bender and cutter was operated. Relevant Construction Noise Permit GW-RS1366-13 was in place while it is considered that there is no sufficient information to indicate whether the Powered Mechanical Equipment were deployed at the designed location stipulated under the relevant Construction Noise Permit with noise mitigation measures required.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Nevertheless, further to the joint ad-hoc inspection conducted by the ET/IEC on 13 February 2017 during restricted hours (between 1900hrs to 2200hrs), concurrent operations of 4 nos. of concrete lorry trucks at the Southern Side of TS3 near Construction Site Entrance and concurrent operations of 2 nos. of concrete lorry pumps and 2 nos. of concrete lorry truck at Western and Northern Side of TS3 were observed while the temporary noise barrier provided for the concrete lorry pump and concrete lorry truck at the Northern Side of TS3 could not screen entirely the concrete lorry truck and concrete lorry pump (Located at Northern Side of TS3) from nearby sensitive receivers. Therefore, it is considered that the above operations observed could not follow the PME grouping requirement and the specific condition 3.d.4 under the relevant Construction Noise Permit. In view of the above, the Contractor of HY/2010/08 was advised to enhance the site supervision and strictly implement the site control system for construction works carried out during restricted hours to ensure the PMEs deployed strictly comply with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC complaint case (Ref: #2-3521097579) dated 22 February 2017	22 February 2017	ICC complaint case referred by RSS received by ET on 27 February 2017	Construction Site at Victoria Harbour near Victoria Park	Noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.	An ICC complaint referred by RSS was received by ET on 27 February 2017 (CASE#2-3521097579). The complainant reported that noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene. ET confirmed with the Resident Site Staff that no construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017. No construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	Final Investigation Report issued on 02 March 2017 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC Complaint Case (CASE #2-357615753 8 dated 05 March 2017)	05 March 2017	ICC complaint referred by RSS was received by ET on 06 March 2017	Construction works area under Contract HK/2009/02 for Wanchai Development Phase II	Noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.	An ICC complaint referred by RSS was received by ET on 06 March 2017 (CASE#2-3576157538). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected. ET confirmed with the Resident Site Staff that no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 no. of loader were in operation below ground level. According to the information confirmed by RSS, no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 loader were in operation below	Investigation report issued on 10 March 2017 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					ground level. Relevant Construction Noise Permit GW-RS1305-16 was in place. Nevertheless, in view of the public concern, the Contractor of HK/2009/02 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HK/2009/02 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
EPD complaint (Case Ref: H05/RS/00 06240-17)	05 March 2017	EPD complaint referred by RSS was received by ET on 14 March 2017. EPD clarified the complaint case shall be referred by ICC Complaint Hotline (CASE #2-3576157538)	Construction works area under Contract HK/2009/02 for Wanchai Development Phase II	Noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.	A EPD complaint was referred to the ET on 14 March 2017 (CASE Ref: H05/RS/0006240-17). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected. ET confirmed with the Resident Site Staff that no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 no. of loader were in operation below ground level.	Interim Investigation report issued on 10 March 2017 and case closed. Under EPD Review.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to the information confirmed by RSS, no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 loader were in operation below ground level. Relevant Construction Noise Permit GW-RS1305-16 was in place. Nevertheless, in view of the public concern, the Contractor of HK/2009/02 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HK/2009/02 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
ICC complaint Case (CASE#2-3603182890) dated 10 March 2017	10 March 2017	An ICC complaint referred by RSS was received by ET on 13 March 2017	Construction Site at Victoria Park	Noise was emanated from the construction Site at Victoria Park from 2300hrs to 2400hrs on 10 March 2017 and caused nuisance to nearby residents.	An ICC complaint referred by RSS was received by ET on 13 March 2017 (CASE#2-3603182890). The complainant reported that noise was emanated from the construction Site at Victoria Park from 2300hrs to 2400hrs on 10 March 2017 and caused nuisance to nearby residents. ET confirmed with the Resident Site Staff that no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.	Investigation Report issued on 15 March 2017 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Based on the information provided by the RSS, no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
EPD complaint Case (CASE Ref: H05/RS/00 014415-17(14448-17) dated 18 May 2017	11 May 2017	An EPD complaint referred to ET on 18 May 2017	Construction Site under Contract HK/2009/02	Construction work was found on 10 May 2017 (~03:52) that caused noise nuisance. According to the information provided by the IEC on 11 May 2017 and 15 May 2017, it was alleged that the concreting work under Contract No. HK/2009/02 was carried out for the Central-Wan Chai Bypass Top Slab Bay 6 during night time on 09 May 2017 and early morning on 10 May 2017 (between 11:00pm on 09 May 2017 and about 04:00 a.m. on 10 May 2017) with 3 pump trucks, 10 vibrating pokers, 9 concrete trucks and 2 generators in operation.	An EPD complaint was referred to the ET on 18 May 2017 (CASE Ref: H05/RS/00014415-17(14448-17). The complainant reported that: Construction work was found on 10 May 2017 (~03:52) that caused noise nuisance. According to the photos provided by the complainant lorry mounted concrete pump were used. According to the information provided by the IEC on 11 May 2017 and 15 May 2017, it was alleged that the concreting work under Contract No. HK/2009/02 was carried out for the Central-Wan Chai Bypass Top Slab Bay 6 during night time on 09 May 2017 and early morning on 10 May 2017 (between 11:00pm on 09 May 2017 and about 04:00 a.m. on 10 May 2017) with 3 pump trucks, 10 vibrating pokers, 9 concrete trucks and 2 generators in operation. The concreting works under Contract No. CEDD HK/2009/02 was also carried out for the Central – Wan Chai Bypass Bay 10A OHVS Slab after 23:00 on 12 May 2017 (after 23:00) with 1 Pump truck, 2 vibrating pokers, 1 concrete trucks and 3 generators in operation.	Investigation report submitted to EPD on 26 May 2017.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				The concreting works under Contract No. CEDD HK/2009/02 was also carried out for the Central – Wan Chai Bypass Bay 10A OHVS Slab after 23:00 on 12 May 2017 (after 23:00) with 1 Pump truck, 2 vibrating pokers, 1 concrete trucks and 3 generators in operation.	ET confirmed with the Resident Site Staff that 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017. 2 nos. of vibratory pokers, 1 no. of concrete truck, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017. According to the RSS site information, 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generator were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 11 May 2017, ad-hoc inspection was conducted by the Environmental Team on 13 May 2017 around 00:40 hrs. No construction operation and no PME deployment was observed at the time of inspection. According to the RSS site information, 2 nos. of vibratory pokers, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017 and could not comply with the item 3a - PME requirement under Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 15 May 2017, ad-hoc inspection was conducted by the Environmental Team on 19 May	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					2017 around 22:20hrs. 2 nos. of concrete truck, 1 no. of concrete pump truck were observed in operation at the time of inspection and relevant CNP GW-RS0334-17 was in place. Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Contractor of HK/2009/02 is also recommended to provide briefing and training session to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/2009/02 during restricted hours and report relevant findings, if any, accordingly.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD complaint Case (CASE Ref: N/A) dated 23 May 2017	23 May 2017	An EPD complaint referred to ET on 25 May 2017	Construction Site under Contract HK/2009/02	Concreting works under Contract No. CEDD HK/2009/02 was carried out with crawler cranes, 10-12 vibratory pokers, and 7 concrete lorry mixers in the morning on 21 May 2017 without a valid CNP. Also, at 15:30 on 21 May 2017, 9 vibratory pokers and 7 concrete lorry mixers were observed in operation. These works were suspected to contravene the Noise Control Ordinance (NCO).	An EPD complaint was referred to the ET on 25 May 2017 (CASE Ref: N/A). The complainant reported that concreting works under Contract No. CEDD HK/2009/02 was carried out with crawler cranes, 10-12 vibratory pokers, and 7 concrete lorry mixers in the morning on 21 May 2017 without a valid CNP. Also, at 15:30 on 21 May 2017, 9 vibratory pokers and 7 concrete lorry mixers were observed in operation. These works were suspected to contravene the Noise Control Ordinance (NCO). ET confirmed with the Resident Site Staff that 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017. 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs on 21 May 2017. 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 7 nos. of concreting trucks were operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017. According to the RSS site information, the following PME were operated on 21 May 2017, i) 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs; ii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs; iii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017; iv) 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs; v) 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs ; 7 nos. of concreting trucks were	Investigation report submitted to EPD on 02 June 2017.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS334-17. EPD notification on the cancellation of the Construction Noise Permits GW-RS0334-17 and Construction Noise Permit GW-RS1297-16 was received by the Environmental Team on 26 May 2017. Ad hoc inspection was conducted by the Environmental Team on 26 May 2017 around 2230hrs and on 28 May 2017 around 1520hrs and no construction works and no operation of PME was observed at the concerned site Portion 5 at the time of inspections. Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Contractor of HK/2009/02 is also recommended to provide briefing and training section to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours.	



Appendix 6.2

Summary for Notification of Exceedance



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A043	2-Mar-17	8:00	CMA5b- Pedestrian Plaza	287.3	24hr TSP (ug/m ³)	181.0	260	Possible reason: Elevated TSP level potentially in relate to ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: Despite ground paving by concrete and plant mobilization were undertaken on the monitoring date at the Central Ventilation Building under Contractor of HY/2011/08, no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 02 to 03 March 2017 was recorded as ranged from 5 - 6). In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. Nevertheless, the Contractor of HY/2011/08 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A032	2-Mar-17	8:00	CMA5b- Pedestrian Plaza	287.3	24hr TSP (ug/m ³)	181.0	260	Possible reason: Elevated TSP level potentially in relate to ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Mitigation measures including maintaining haul road in dampened condition was implemented by contractor. Remarks / Other Obs: Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition was implemented and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 02 to 03 March 2017 was recorded as ranged from 5 - 6). In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. In addition, non WDII-CWVB Project construction activities opposite to the monitoring station was observed on the monitoring date. Nevertheless, the Contractor of HK/2012/08 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A034	2-Mar-17	8:00	CMA5b- Pedestrian Plaza	287.3	24hr TSP (ug/m ³)	181.0	260	Possible reason: Elevated TSP level potentially in relate to ambient environment and other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: No construction works was undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2009/01 and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 02 to 03 March 2017 was recorded as ranged from 5 - 6). In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. Nevertheless, the Contractor of HK/2009/01 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A044	3-Mar-17	8:02	CMA5b- Pedestrian Plaza	393.5	1hr TSP (ug/m ³)	339.7	500	Possible reason: Elevated TSP level potentially in relate to ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: Despite ground paving by concrete and plant mobilization were undertaken on the monitoring date at the Central Ventilation Building under Contractor of HY/2011/08, no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HY/2011/08 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.
X_16A045	3-Mar-17	9:30	CMA5b- Pedestrian Plaza	348.1	1hr TSP (ug/m ³)	339.7	500	Possible reason: Elevated TSP level potentially in relate to other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: Despite ground paving by concrete and plant mobilization were undertaken on the monitoring date at the Central Ventilation Building under Contractor of HY/2011/08, no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HY/2011/08 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.
X_16A046	3-Mar-17	13:00	CMA5b- Pedestrian Plaza	826.4	1hr TSP (ug/m ³)	339.7	500	Possible reason: Elevated TSP level potentially in relate to other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: Despite ground paving by concrete and plant mobilization were undertaken on the monitoring date at the Central Ventilation Building under Contractor of HY/2011/08, no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HY/2011/08 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A035	3-Mar-17	8:02	CMA5b- Pedestrian Plaza	393.5	1hr TSP (ug/m ³)	332.0	500	Possible reason: Elevated TSP level potentially in relate to ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Mitigation measures including maintaining haul road in dampened condition was implemented by contractor. Remarks / Other Obs: Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition were implemented and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HK/2012/08 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.
X_16A036	3-Mar-17	9:30	CMA5b- Pedestrian Plaza	348.1	1hr TSP (ug/m ³)	332.0	500	Possible reason: Elevated TSP level potentially in relate to other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Mitigation measures including maintaining haul road in dampened condition was implemented by contractor. Remarks / Other Obs: Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition were implemented and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HK/2012/08 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.
X_16A037	3-Mar-17	13:00	CMA5b- Pedestrian Plaza	826.4	1hr TSP (ug/m ³)	332.0	500	Possible reason: Elevated TSP level potentially in relate to other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Mitigation measures including maintaining haul road in dampened condition was implemented by contractor. Remarks / Other Obs: Despite concreting, formwork erection and rebar fixing were undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2012/08, dust suppression measure including haul road maintained in dampened condition were implemented and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HK/2012/08 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A038	3-Mar-17	8:02	CMA5b- Pedestrian Plaza	393.5	1hr TSP (ug/m ³)	332.0	500	Possible reason: Elevated TSP level potentially in relate to ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: No construction works was undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2009/01 and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HK/2009/01 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.
X_16A039	3-Mar-17	9:30	CMA5b- Pedestrian Plaza	348.1	1hr TSP (ug/m ³)	332.0	500	Possible reason: Elevated TSP level potentially in relate to other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: No construction works was undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2009/01 and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HK/2009/01 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.
X_16A040	3-Mar-17	13:00	CMA5b- Pedestrian Plaza	826.4	1hr TSP (ug/m ³)	332.0	500	Possible reason: Elevated TSP level potentially in relate to other sources affecting local ambient condition such as road traffic next to the monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: No construction works was undertaken on the monitoring date at around Pedestrian Plaza under Contractor of HK/2009/01 and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed across the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period on 03 March 2017 was recorded at 6) and elevated TSP level was observed across other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project construction activities opposite to the monitoring station was observed on the monitoring date. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and other sources affecting local ambient condition such as road traffic next to the monitoring station. Nevertheless, the Contractor of HK/2009/01 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A031	3-Mar-17	13:00	CMA4a- SPCA	939.9	1hr TSP (ug/m ³)	312.0	500	Possible reason: Elevated TSP level potentially in relate to ambient air quality and non WDII-CWB renovation works next to the monitoring station. Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Mitigation measures including covering of stockpile and watering for haul road and during loading and unloading of material were implemented by the Contractor Remarks / Other Obs: Despite backfilling works at Portion 3&4 and tunnel structure works at Portion 5 were conducted on 03 March 2017 on the monitoring date around the monitoring station under Contractor of HK/2009/02, dust suppression measure including covering of stockpile and watering for haul road and during loading and unloading of material were implemented by the Contractor and no particular observation regarding air quality impact was observed during sampling. Meanwhile, severe smog was reported observed accross the period on 01 March 2017 and it is considered that exceedance was potentially in relate to the residual effect of the severe smog observed (AQHI at Eastern District Station during monitoring period was recorded at 6 on 03 March 2017 during monitoring period). Also, elevated TSP level was observed accross other monitoring stations from Wanchai to North Point Districts on the same monitoring date. In addition, non WDII-CWB Project renovation works was conducted next to the monitoring station. In view of the above, the exceedance was considered to be non-project related and potentially contributed by ambient air quality and the observed renovation works next to the monitoring station. Nevertheless, the Contractor of HK/2009/02 was reminded to maintain regularly dust suppression measures for any potential dusty surface and dust generating operation around the concerned location to avoid any potential cumulative air quality impact.



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A048	27-Mar-17	10:35	CMA1b- Oil Street Site Office	570.6	1 hr TSP (ug/m ³)	320.1	500	Possible reason: Elevated TSP level in relate to local ambient condition around monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: Concrete and bar fixing works was undertaken under Contract HY/2011/08 on the monitoring date at around Oil Street Site Office while regular water spraying on ground was generally implemented by the Contractor and no particular observation regarding air quality impact was observed during sampling. In view of the above, the limit level exceedance was considered to be non-project related and contributed by local ambient condition.



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_16A047	27-Mar-17	10:35	CMA1b- Oil Street Site Office	570.6	1 hr TSP (ug/m ³)	320.1	500	Possible reason: Elevated TSP level in relate to local ambient condition around monitoring station Action taken / to be taken: Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures. Remarks / Other Obs: No construction works was undertaken under Contract HY/2009/19 on the monitoring date at around Oil Street Site Office while the haul road around the concerned location was observed maintained in dampened condition and no particular observation regarding air quality impact was observed during sampling. In view of the above, the limit level exceedance was considered to be non-project related and contributed by local ambient condition.

Ref. No.	Date	Time	Location	Construction Noise Level, dB(A)	Parameter	Action Level	Limit Level dB(A)	Follow-up action
X_16N063	3-Apr-17	9:45	M6 - HK Baptist Church Henrietta Secondary School	70	Leq(30min)	when one documented complaint was received.	65	Possible reason: Traffic nearby was observed during monitoring and was considered as the major noise contribution. Action taken / to be taken: Repeated measurement to confirm result and reviewed the trend of noise measurement. Analysis of contractor's working procedure. Remarks / Other Obs: Despite scaffold erection by crane was undertaken by Contractor of HY/2009/19, no particular noise was considered from the construction activities and nearby traffic noise was observed as major noise source during monitoring. As such, the exceedance was considered as non-Project related.
X_16N064	10-Apr-17	9:26	M6 - HK Baptist Church Henrietta Secondary School	68	Leq(30min)	when one documented complaint was received.	65	Possible reason: Traffic nearby was observed during monitoring and was considered as the major noise contribution. Action taken / to be taken: Repeated measurement to confirm result and reviewed the trend of noise measurement. Analysis of contractor's working procedure. Remarks / Other Obs: Despite rebar fixing by crane was undertaken by Contractor of HY/2009/19, no particular noise was considered from the construction activities and nearby traffic noise was observed as major noise source during monitoring. As such, the exceedance was considered as non-Project related.
X_10N145	18-Apr-17	13:50	M5b - City Garden	78	N/A	when one documented complaint was received.	75	Possible reason: Breaking works at marine pier was observed as the major noise contribution during measurement. Mitigation measures including temporary noise barrier was observed provided but opening was observed at the temporary noise barrier system. Action taken / to be taken: Immediate repeat measurement was conducted to confirm the result at the same location. The construction noise level of repeated measurement at the same location on the same date was: 18 April 2017 at 14:20 76 dB(A). Contractor was advised to prepare and submit the remediation plan for the concerned construction works. Remarks / Other Obs: Remedial actions including i) closing the opening of the temporary noise barrier ii) provide physical wrapping of breaker to dampen noise emission and iii) conduct breaking works intermittently were implemented by the Contractor and additional monitoring was conducted on 19 April 2017. The construction noise level during additional monitoring was found to be 19 April 2017 at 15:10 71 dB(A). No further exceedance was recorded. Starter bar fixing works and breaking works at marine pier under Contract HY/2009/19 was conducted during the measurement on 18 April 2017, it was observed that breaking operation was the major noise contribution during measurement. It is concluded that the exceedance was Project related and the contractor was requested to submit a proposal for remediation measures following the Event and Action Plan. Actions from the remediation plan including i) Closing the opening of the temporary noise barrier ii) provide physical wrapping of breaker to dampen noise emission and iii) conduct breaking works intermittently were implemented by the Contractor and no further exceedance was recorded upon implementation of the remedial actions
X_16N065	26-Apr-17	14:30	M6 - HK Baptist Church Henrietta Secondary School	68	Leq(30min)	when one documented complaint was received.	65	Possible reason: Traffic nearby was observed during monitoring and was considered as the major noise contribution. Action taken / to be taken: Repeated measurement to confirm result and reviewed the trend of noise measurement. Analysis of contractor's working procedure. Remarks / Other Obs: Despite formwork erection for upstanding wall was undertaken by Contractor of HY/2009/19, no particular noise was considered from the construction activities and nearby traffic noise was observed as major noise source during monitoring. As such, the exceedance was considered as non-Project related.

Ref. No.	Date	Time	Location	Construction Noise Level, dB(A)	Parameter	Action Level	Limit Level dB(A)	Follow-up action
X_16N068	16-May-17	13:48	M1a-Harbour Road Sports Centre	77	Leq(30min)	when one documented complaint was received.	75	Possible reason: Breaking and drilling operation next to the monitoring station under non WDII-CWB Contractor was observed as the major noise contribution. Action taken / to be taken: A repeat measurement was conducted to confirm result and reviewed the trend of previous noise monitoring and Contractor's working procedure. Remarks / Other Obs: Re-bar and formwork fixing at Portion 5 were conducted under Contract HK/2009/02 around the concerned location during the time of measurement. No major noise was observed from the above construction activities while breaking and drilling operation next to the monitoring station under non WDII-CWB Contractor was observed as the major noise contribution during monitoring. As such, the exceedance was considered as non-Project related.
X_16N069	16-May-17	13:48	M1a-Harbour Road Sports Centre	77	Leq(30min)	when one documented complaint was received.	75	Possible reason: Breaking and drilling next to the monitoring station under non WDII-CWB Contractor was observed as the major noise contribution. Action taken / to be taken: A repeat measurement was conducted to confirm result and reviewed the trend of previous noise monitoring and Contractor's working procedure. Remarks / Other Obs: No construction works was conducted under Contract HK/2009/01 during the time of measurement while breaking and drilling operation next to the monitoring station under non WDII-CWB Contractor was observed as the major noise contribution during monitoring. As such, the exceedance was considered as non-Project related.
X_16N071	25-May-17	10:45	M1a-Harbour Road Sports Centre	77	Leq(30min)	when one documented complaint was received.	75	Possible reason: Bored piling works next to the monitoring station under non WDII-CWB Contractor was observed as the major noise contribution. Action taken / to be taken: A repeat measurement was conducted to confirm result and reviewed the trend of previous noise monitoring and Contractor's working procedure. Remarks / Other Obs: Re-bar fixing at Portion 5 was conducted under Contract HK/2009/02 around the concerned location during the time of measurement. No major noise was observed from the above construction activities while bored piling works next to the monitoring station under non WDII-CWB Contractor was observed as the major noise contribution during monitoring. As such, the exceedance was considered as non-Project related.
X_16N072	25-May-17	10:45	M1a-Harbour Road Sports Centre	77	Leq(30min)	when one documented complaint was received.	75	Possible reason: Bored piling works next to the monitoring station under non WDII-CWB Contractor was observed as the major noise contribution. Action taken / to be taken: A repeat measurement was conducted to confirm result and reviewed the trend of previous noise monitoring and Contractor's working procedure. Remarks / Other Obs: No construction works was conducted under Contract HK/2009/01 during the time of measurement while bored piling works next to the monitoring station under non WDII-CWB Contractor was observed as the major noise contribution during monitoring. As such, the exceedance was considered as non-Project related.



Appendix 8.1

Construction Programme of Individual Contracts

Contract No. HK/2009/01
Wan Chai Development Phase II – Central -Wan Chai Bypass at
Hong Kong Convention and Exhibition Centre

Construction Activities For Three Months Rolling

Construction Activities	Dec 2016	Jan 2017	Feb 2017	Mar 2017	Apr 2017
Reinstatement of Amenity Area					
Road and Drain Works					

Contract No. HK/2009/01

Wan Chai Development Phase II – Central -Wan Chai Bypass at
Hong Kong Convention and Exhibition Centre

Construction Activities for Three Months Rolling

Construction Activities	May 2017	June 2017	July 2017
Reinstatement of Amenity Area			
Road and Drain Works			

Activity ID	Activity Name	On Dur	Rem Dur	Scheduled/ Actual Start	Scheduled/ Actual Finish	Total Float	Calendar	2016																					
								January				February				March				April									
								25	01	08	15	22	29	05	12	19	26	05	12	19	26	02	09	16					
Three Months Rolling Programme 2017-01-20 (dd 20-Jan-17)																													
Programme Milestones (Revised up to EOTO No.21)																													
Contractual Completion Dates																													
KDC0170	Section 9B Works (2107 days) - CWB Structure (CH3400 Eastward) (2-Dec-15 Noon)	0	0		20-Jan-17*	-114	Calendar Day																	◆ Section 9B Works (2107 days) - CWB Structure (CH3400 Eastward) (2-Dec-15 Noon)					
KDC0180	Section 10 Works (2197 days) - CWB Structure (CH3400 Westward) (20-Oct-16 Noon)	0	0		20-Jan-17*	-91	Calendar Day																	◆ Section 10 Works (2197 days) - CWB Structure (CH3400 Westward) (20-Oct-16 Noon)					
KDC0190	Section 11 Works (2407 days) - Remainder of Works/ Works Completion Date (19-May-17 Noon)	0	0		19-May-17*	0	Calendar Day																						
Soft Landscaping & Establishment Key Dates																													
KDC0200	Section 11A Works (2437 days) - Remaining Landscape Softworks (03-Oct-16 Noon)	0	0		20-Jan-17*	-108	Calendar Day																	◆ Section 11A Works (2437 days) - Remaining Landscape Softworks (03-Oct-16 Noon)					
Section 8A of the Works - Reprovisioning of Wan Chai Ferry Pier in Area 8																													
Outstanding Works																													
S8A-OUT-1060	Reinstatement works of the flooring inside the rooms under staircase ST-01 of the Ferry Pier	12	12	04-Mar-17	16-Mar-17	49	HK Working Day																	■ Reinstatement works of the flooring inside the rooms under staircase ST-01 of the Ferry Pier					
S8A-OUT-1070	Reinstatement works of the flooring under the temporary covered walkway	6	6	17-Mar-17	23-Mar-17	49	HK Working Day																	■ Reinstatement works of the flooring under the temporary covered walkway					
Section 9B of the Works - CWB Tunnel Structure (CH3400 - CH3796)																													
Tunnel Portion 1 (CH3500-CH3630)																													
CWB Structural Works																													
Outstanding Works																													
S9B-T1-OUT-1010	TB1 - Remedial works of the cross road ducts	25	34	12-Oct-16 A	22-Feb-17	-473	Calendar Day																	■ TB1 - Remedial works of the cross road ducts, TB1 - Remedial works of the cross road ducts					
S9B-T1-OUT-1020	TB1 - Remedial works of the OHVD damper openings and base slab levels found out-of-tolerance	25	25	23-Feb-17	19-Mar-17	-473	Calendar Day																	■ TB1 - Remedial works of the OHVD damper openings and base slab levels found out-of-tolerance					
Tunnel Portion 2 (CH3425-CH3500)																													
CWB Structural Works																													
Outstanding Works																													
S9B-T2-OUT-1010	TB2 - Remedial works of the cross road ducts	25	34	12-Oct-16 A	22-Feb-17	-448	Calendar Day																	■ TB2 - Remedial works of the cross road ducts, TB2 - Remedial works of the cross road ducts					
Tunnel Portion 3 & Tunnel Portion 4 (CH3630-CH3790)																													
CWB Structural Works																													
Outstanding Works																													
S9B-T3-OUT-1020	TP3 & 4 - Carry out defects rectification works	25	64	05-Oct-16 A	24-Mar-17	-478	Calendar Day																	■ TP3 & 4 - Carry out defects rectification works, TP3 & 4 - Carry out defects rectification works					
S9B-T3-OUT-1030	TP3 & 4 - Remedial works of the cross road ducts	18	58	12-Oct-16 A	18-Mar-17	-472	Calendar Day																	■ TP3 & 4 - Remedial works of the cross road ducts, TP3 & 4 - Remedial works of the cross road ducts					
Tunnel Portion 5 (CH3400-CH3425)																													
Bay 13 (Eastern End Bay)																													
S9B-T5-B13-1010	Base Slab - Waterproofing	4	14	06-Jan-17 A	02-Feb-17	-590	Calendar Day																	■ Base Slab - Waterproofing, Base Slab - Waterproofing					
S9B-T5-B13-1020	Base Slab - Rebar Fixing	10	10	13-Feb-17	22-Feb-17	-590	Calendar Day																	■ Base Slab - Rebar Fixing, Base Slab - Rebar Fixing					
S9B-T5-B13-1030	Base Slab - Concrete	1	1	23-Feb-17	23-Feb-17	-590	Calendar Day																	■ Base Slab - Concrete, Base Slab - Concrete					
S9B-T5-B13-1040	Base Slab - Curing	4	4	24-Feb-17	27-Feb-17	-590	Calendar Day																	■ Base Slab - Curing, Base Slab - Curing					
S9B-T5-B13-1050	Wall (North) - Waterproofing & Working Platform	4	4	12-Mar-17	15-Mar-17	-548	Calendar Day																	■ Wall (North) - Waterproofing & Working Platform, Wall (North) - Waterproofing & Working Platform					
S9B-T5-B13-1060	Wall (North) - Rebar Fixing	3	3	16-Mar-17	18-Mar-17	-548	Calendar Day																	■ Wall (North) - Rebar Fixing, Wall (North) - Rebar Fixing					
S9B-T5-B13-1070	Wall (North) - Formwork	2	2	25-Apr-17	26-Apr-17	-585	Calendar Day																	■ Wall (North) - Formwork, Wall (North) - Formwork					
S9B-T5-B13-1100	Wall (South) - Waterproofing & Working Platform	4	4	12-Mar-17	15-Mar-17	-548	Calendar Day																	■ Wall (South) - Waterproofing & Working Platform, Wall (South) - Waterproofing & Working Platform					
S9B-T5-B13-1110	Wall (South) - Rebar Fixing	3	3	16-Mar-17	18-Mar-17	-548	Calendar Day																	■ Wall (South) - Rebar Fixing, Wall (South) - Rebar Fixing					
S9B-T5-B13-1150	Wall (Middle) - Rebar Fixing & Working Platform	4	4	12-Mar-17	15-Mar-17	-545	Calendar Day																	■ Wall (Middle) - Rebar Fixing & Working Platform, Wall (Middle) - Rebar Fixing & Working Platform					
Bay 12																													
S9B-T5-B12-1020	Base Slab - Rebar Fixing	10	2	09-Jan-17 A	21-Jan-17	-558	Calendar Day																	■ Base Slab - Rebar Fixing, Base Slab - Rebar Fixing					
S9B-T5-B12-1030	Base Slab - Concrete	1	1	22-Jan-17	22-Jan-17	-558	Calendar Day																	■ Base Slab - Concrete, Base Slab - Concrete					
S9B-T5-B12-1040	Base Slab - Curing	4	4	23-Jan-17	26-Jan-17	-558	Calendar Day																	■ Base Slab - Curing, Base Slab - Curing					
S9B-T5-B12-1050	Wall (North) - Waterproofing & Working Platform	4	4	12-Mar-17	15-Mar-17	-558	Calendar Day																	■ Wall (North) - Waterproofing & Working Platform, Wall (North) - Waterproofing & Working Platform					
S9B-T5-B12-1060	Wall (North) - Rebar Fixing	3	3	16-Mar-17	18-Mar-17	-554	Calendar Day																	■ Wall (North) - Rebar Fixing, Wall (North) - Rebar Fixing					
S9B-T5-B12-1070	Wall (North) - Formwork	2	2	19-Apr-17	20-Apr-17	-585	Calendar Day																	■ Wall (North) - Formwork, Wall (North) - Formwork					
S9B-T5-B12-1080	Wall (North) - Concrete	1	1	21-Apr-17	21-Apr-17	-585	Calendar Day																	■ Wall (North) - Concrete, Wall (North) - Concrete					
S9B-T5-B12-1090	Wall (North) - Curing & Formwork Dismantling	3	3	22-Apr-17	24-Apr-17	-585	Calendar Day																	■ Wall (North) - Curing & Formwork Dismantling, Wall (North) - Curing & Formwork Dismantling					
S9B-T5-B12-1100	Wall (South) - Waterproofing & Working Platform	4	4	16-Mar-17	19-Mar-17	-558	Calendar Day																	■ Wall (South) - Waterproofing & Working Platform, Wall (South) - Waterproofing & Working Platform					
S9B-T5-B12-1110	Wall (South) - Rebar Fixing	3	3	20-Mar-17	22-Mar-17	-558	Calendar Day																	■ Wall (South) - Rebar Fixing, Wall (South) - Rebar Fixing					
S9B-T5-B12-1120	Wall (South) - Formwork	2	2	23-Apr-17	24-Apr-17	-589	Calendar Day																	■ Wall (South) - Formwork, Wall (South) - Formwork					
S9B-T5-B12-1130	Wall (South) - Concrete	1	1	25-Apr-17	25-Apr-17	-589	Calendar Day																	■ Wall (South) - Concrete, Wall (South) - Concrete					
S9B-T5-B12-1140	Wall (South) - Curing & Formwork Dismantling	3	3	26-Apr-17	28-Apr-17	-589	Calendar Day																	■ Wall (South) - Curing & Formwork Dismantling, Wall (South) - Curing & Formwork Dismantling					
S9B-T5-B12-1150	Wall (Middle) - Rebar Fixing & Working Platform	4	4	27-Jan-17	30-Jan-17	-507	Calendar Day																	■ Wall (Middle) - Rebar Fixing & Working Platform, Wall (Middle) - Rebar Fixing & Working Platform					
								Date																Revision		Checked		Approved	
																								Rev. Programme (08.12.16)					

[illegible]

Activity ID	Activity Name	Oa Dur	Rem Dur	Scheduled Actual Start	Scheduled Actual Finish	Total Float	Calendar	2017																											
								January				February				March				April				May											
								25	01	08	15	22	29	05	12	19	26	05	12	19	26	02	09	16	23	30	06	13	20	27					
S10-TS-B8-1160	Wall (Middle) - Formwork	2	2	19-Feb-17	20-Feb-17	-475	Calendar Day																												
S10-TS-B8-1170	Wall (Middle) - Concrete	1	1	21-Feb-17	21-Feb-17	-475	Calendar Day																												
S10-TS-B8-1180	Wall (Middle) - Curing & Formwork Dismantling	3	3	22-Feb-17	24-Feb-17	-475	Calendar Day																												
S10-TS-B8-1185	Construct Roadside Barriers	7	7	05-Apr-17	11-Apr-17	-496	Calendar Day																												
S10-TS-B8-1230	OHVD Base Slab (North) - Scaffolding Erection	10	10	12-Apr-17	21-Apr-17	-399	Calendar Day																												
S10-TS-B8-1240	OHVD Base Slab (North) - Formwork & Rebar Fixing	7	7	22-Apr-17	28-Apr-17	-396	Calendar Day																												
S10-TS-B8-1270	OHVD Base Slab (South) - Scaffolding Erection	10	10	22-Apr-17	01-May-17	-399	Calendar Day																												
Bay 8																																			
S10-TS-B8-1050	Wall (North) - Waterproofing & Working Platform	4	4	16-Feb-17	19-Feb-17	-552	Calendar Day																												
S10-TS-B8-1060	Wall (North) - Rebar Fixing	3	3	20-Feb-17	22-Feb-17	-548	Calendar Day																												
S10-TS-B8-1070	Wall (North) - Formwork	2	2	01-Apr-17	02-Apr-17	-585	Calendar Day																												
S10-TS-B8-1080	Wall (North) - Concrete	1	1	03-Apr-17	03-Apr-17	-585	Calendar Day																												
S10-TS-B8-1090	Wall (North) - Curing & Formwork Dismantling	3	3	04-Apr-17	06-Apr-17	-585	Calendar Day																												
S10-TS-B8-1100	Wall (South) - Waterproofing & Working Platform	4	4	20-Feb-17	23-Feb-17	-552	Calendar Day																												
S10-TS-B8-1110	Wall (South) - Rebar Fixing	3	3	24-Feb-17	26-Feb-17	-552	Calendar Day																												
S10-TS-B8-1120	Wall (South) - Formwork	2	2	05-Apr-17	06-Apr-17	-589	Calendar Day																												
S10-TS-B8-1130	Wall (South) - Concrete	1	1	07-Apr-17	07-Apr-17	-589	Calendar Day																												
S10-TS-B8-1140	Wall (South) - Curing & Formwork Dismantling	3	3	08-Apr-17	10-Apr-17	-589	Calendar Day																												
S10-TS-B8-1150	Wall (Middle) - Rebar Fixing & Working Platform	3	3	20-Jan-17	22-Jan-17	-436	Calendar Day																												
S10-TS-B8-1160	Wall (Middle) - Formwork	2	2	25-Feb-17	26-Feb-17	-469	Calendar Day																												
S10-TS-B8-1170	Wall (Middle) - Concrete	1	1	27-Feb-17	27-Feb-17	-469	Calendar Day																												
S10-TS-B8-1180	Wall (Middle) - Curing & Formwork Dismantling	3	3	28-Feb-17	02-Mar-17	-469	Calendar Day																												
S10-TS-B8-1185	Construct Roadside Barriers	7	7	11-Apr-17	17-Apr-17	-502	Calendar Day																												
S10-TS-B8-1230	OHVD Base Slab (North) - Scaffolding Erection	10	10	18-Apr-17	27-Apr-17	-412	Calendar Day																												
Bay 7																																			
S10-TS-B7-1050	Wall (North) - Waterproofing & Working Platform	4	4	08-Feb-17	11-Feb-17	-578	Calendar Day																												
S10-TS-B7-1060	Wall (North) - Rebar Fixing	3	3	12-Feb-17	14-Feb-17	-534	Calendar Day																												
S10-TS-B7-1070	Wall (North) - Formwork	2	2	07-Apr-17	08-Apr-17	-585	Calendar Day																												
S10-TS-B7-1080	Wall (North) - Concrete	1	1	09-Apr-17	09-Apr-17	-585	Calendar Day																												
S10-TS-B7-1090	Wall (North) - Curing & Formwork Dismantling	3	3	10-Apr-17	12-Apr-17	-585	Calendar Day																												
S10-TS-B7-1100	Wall (South) - Waterproofing & Working Platform	4	4	12-Feb-17	15-Feb-17	-538	Calendar Day																												
S10-TS-B7-1110	Wall (South) - Rebar Fixing	3	3	16-Feb-17	18-Feb-17	-538	Calendar Day																												
S10-TS-B7-1120	Wall (South) - Formwork	2	2	11-Apr-17	12-Apr-17	-589	Calendar Day																												
S10-TS-B7-1130	Wall (South) - Concrete	1	1	13-Apr-17	13-Apr-17	-589	Calendar Day																												
S10-TS-B7-1140	Wall (South) - Curing & Formwork Dismantling	3	3	14-Apr-17	16-Apr-17	-589	Calendar Day																												
S10-TS-B7-1150	Wall (Middle North) - Rebar Fixing & Working Platform	3	3	08-Feb-17	10-Feb-17	-449	Calendar Day																												
S10-TS-B7-1160	Wall (Middle North) - Formwork	2	2	09-Apr-17	10-Apr-17	-506	Calendar Day																												
S10-TS-B7-1170	Wall (Middle North) - Concrete	1	1	11-Apr-17	11-Apr-17	-506	Calendar Day																												
S10-TS-B7-1180	Wall (Middle North) - Curing & Formwork Dismantling	3	3	12-Apr-17	14-Apr-17	-506	Calendar Day																												
S10-TS-B7-1185	Construct Roadside Barriers	7	7	17-Apr-17	23-Apr-17	-508	Calendar Day																												
S10-TS-B7-1190	Wall (Middle South) - Rebar Fixing & Working Platform	3	3	18-Jan-17 A	22-Jan-17	-511	Calendar Day																												
S10-TS-B7-1200	Wall (Middle South) - Formwork	2	2	23-Jan-17	24-Jan-17	-511	Calendar Day																												
S10-TS-B7-1210	Wall (Middle South) - Concrete	1	1	25-Jan-17	25-Jan-17	-511	Calendar Day																												
S10-TS-B7-1220	Wall (Middle South) - Curing & Formwork Dismantling	3	3	26-Jan-17	28-Jan-17	-511	Calendar Day																												
S10-TS-B7-1230	OHVD Base Slab (North) - Scaffolding Erection	10	10	24-Apr-17	03-May-17	-392	Calendar Day																												
S10-TS-B7-1310	OHVD Base Slab (South) - Scaffolding Erection	10	10	24-Apr-17	03-May-17	-394	Calendar Day																												
Bay 6																																			
S10-TS-B6-1050	Wall (North) - Waterproofing & Working Platform	4	4	12-Feb-17	15-Feb-17	-578	Calendar Day																												
S10-TS-B6-1060	Wall (North) - Rebar Fixing	3	3	16-Feb-17	18-Feb-17	-578	Calendar Day																												
S10-TS-B6-1070	Wall (North) - Formwork	2	2	01-Mar-17	02-Mar-17	-588	Calendar Day																												
S10-TS-B6-1080	Wall (North) - Concrete	1	1	03-Mar-17	03-Mar-17	-588	Calendar Day																												
S10-TS-B6-1090	Wall (North) - Curing & Formwork Dismantling	3	3	04-Mar-17	06-Mar-17	-588	Calendar Day																												
S10-TS-B6-1100	Wall (South) - Waterproofing & Working Platform	4	4	16-Feb-17	19-Feb-17	-461	Calendar Day																												
S10-TS-B6-1110	Wall (South) - Rebar Fixing	3	3	20-Feb-17	22-Feb-17	-461	Calendar Day																												
S10-TS-B6-1120	Wall (South) - Formwork	2	2	11-Apr-17	12-Apr-17	-508	Calendar Day																												
S10-TS-B6-1130	Wall (South) - Concrete	1	1	13-Apr-17	13-Apr-17	-508	Calendar Day																												
Legend																																			
◆	Milestone																																		
◆	Critical Milestones																																		
■	Current Works																																		
■	Critical Works																																		
■	Remaining Level of Effort																																		
CHUN WO - CRGL								CEDD CONTRACT NO. HK/2009/02								WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)								3-MONTH ROLLING PROGRAMME (dd 20-Jan-17)											
JOINT VENTURE																																			

[illegible]

Activity ID	Activity Name		On Dur	Rem Dur	Scheduled/ Actual Start	Scheduled/ Actual Finish	Total Float	Calendar	2017																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
									2016							January							February							March							April																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
									25	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	01	08	15	22	29	05	12	19	26																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
S10-T5-B4-1180	Wall (Middle North) - Curing & Formwork Dismantling		3	3	26-Jan-17	28-Jan-17	-545	Calendar Day																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					

- ◆ Milestone
- ◆ Critical Milestones
- Current Works
- Critical Works
- Remaining Level of Effort

CHUN WO - CRGL
JOINT VENTURE

CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (dd 20-Jan-17)

Date	Revision	Checked	Approved
	Rev. Programme (08.12.16)		

[illegible]

[illegible]

Activity ID		Activity Name		Ori Dur	Rem Dur	Scheduled/ Actual Start	Scheduled/ Actual Finish	Total Float	Calendar	2017																	
										April				May				June				July					
										26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16	
Three Months Rolling Programme 2017-04-20 (dd 20-Apr-17)																											
Programme Milestones (Revised up to EOTO No.21)																											
Contractual Completion Dates																											
KDC0170	Section 9B Works (2134 days) - CWB Structure (CH3400 Eastward) (2-Dec-15 Noon)	0	0		20-Apr-17*	-504	Calendar Day																				
KDC0180	Section 10 Works (2469 days) - CWB Structure (CH3400 Westward) (31-Oct-16)	0	0		20-Apr-17*	-170	Calendar Day																				
KDC0190	Section 11 Works (2673 days) - Remainder of Works/ Works Completion Date (23-May-17)	0	0		23-May-17*	0	Calendar Day																				
Soft Landscaping & Establishment Key Dates																											
KDC0200	Section 11A Works (2440 days) - Remaining Landscape Softworks (03-Oct-16 Noon)	0	0		20-Apr-17*	-198	Calendar Day																				
KDC0220	Section 12 Works (2672 days) - Protection and Preservation of Existing Trees (22-May-17 Noon)	0	0		22-May-17*	0	Calendar Day																				
Section 8A of the Works - Reprovisioning of Wan Chai Ferry Pier in Area 8																											
Outstanding Works																											
S8A-OUT-1040	Relocation of fire hydrant near Ferry Pier	10	10	14-Jul-17	25-Jul-17	-58	HK Working Day																				
S8A-OUT-1060	Reinstatement works of the flooring inside the rooms under staircase ST-01 of the Ferry Pier	12	12	03-Jul-17	14-Jul-17	-58	HK Working Day																				
S8A-OUT-1070	Reinstatement works of the flooring under the temporary covered walkway	6	6	14-Jul-17	20-Jul-17	-54	HK Working Day																				
Section 8B of the Works - Temporary Covered Walkway & Works in Area 8																											
Temporary Covered Walkway																											
S8B-TCW-02300	Temp Covered Walkway - Construct the remaining Type 4 Covered Walkway at west wing	36	36	17-Jun-17	27-Jul-17	-60	HK Working Day																				
Section 9B of the Works - CWB Tunnel Structure (CH3400 - CH3796)																											
Tunnel Portion 1 (CH3500-CH3630)																											
CWB Structural Works																											
Outstanding Works																											
S9B-T1-OUT-1010	TB1 - Remedial works of the cross road ducts	25	0	12-Oct-16 A	15-Apr-17 A		Calendar Day																				
S9B-T1-OUT-1030	TB1 - Remedial works against water leakage identified inside the OHVD cells	30	0	14-Mar-17 A	12-Apr-17 A		Calendar Day																				
Tunnel Portion 2 (CH3425-CH3500)																											
CWB Structural Works																											
Outstanding Works																											
S9B-T2-OUT-1010	TB2 - Remedial works of the cross road ducts	25	7	12-Oct-16 A	26-Apr-17	-511	Calendar Day																				
S9B-T2-OUT-1020	TB2 - Remedial works against water leakage identified inside the OHVD cells	25	5	12-Oct-16 A	24-Apr-17	29	Calendar Day																				
Tunnel Portion 3 & Tunnel Portion 4 (CH3630-CH3790)																											
CWB Structural Works																											
S9B-T34-7400	ELS (S1) Removal - Bay 1 to Bay 8	28	28	08-Jun-17	06-Jul-17	-503	Calendar Day																				
Tunnel Portion 5 (CH3400-CH3425)																											
Bay 13 (Eastern End Bay)																											
S9B-T5-B13-1020	Base Slab - Rebar Fixing	10	0	11-Feb-17 A	30-Mar-17 A		Calendar Day																				
S9B-T5-B13-1030	Base Slab - Concrete	1	0	31-Mar-17 A	31-Mar-17 A		Calendar Day																				
S9B-T5-B13-1040	Base Slab - Curing	4	0	01-Apr-17 A	04-Apr-17 A		Calendar Day																				
S9B-T5-B13-1050	Wall (North) - Waterproofing & Working Platform	4	0	10-Apr-17 A	14-Apr-17 A		Calendar Day																				
S9B-T5-B13-1060	Wall (North) - Rebar Fixing	3	0	15-Apr-17 A	17-Apr-17 A		Calendar Day																				
S9B-T5-B13-1070	Wall (North) - Formwork	2	0	18-Apr-17 A	19-Apr-17 A		Calendar Day																				
S9B-T5-B13-1080	Wall (North) - Concrete	1	1	20-Apr-17	20-Apr-17	-546	Calendar Day																				
S9B-T5-B13-1090	Wall (North) - Curing & Formwork Dismantling	3	3	21-Apr-17	23-Apr-17	-546	Calendar Day																				
S9B-T5-B13-1100	Wall (South) - Waterproofing & Working Platform	4	0	10-Apr-17 A	13-Apr-17 A		Calendar Day																				
S9B-T5-B13-1110	Wall (South) - Rebar Fixing	3	0	14-Apr-17 A	16-Apr-17 A		Calendar Day																				
S9B-T5-B13-1120	Wall (South) - Formwork	2	0	17-Apr-17 A	18-Apr-17 A		Calendar Day																				
S9B-T5-B13-1130	Wall (South) - Concrete	1	0	19-Apr-17 A	19-Apr-17 A		Calendar Day																				
S9B-T5-B13-1140	Wall (South) - Curing & Formwork Dismantling	3	3	20-Apr-17	22-Apr-17	-549	Calendar Day																				
S9B-T5-B13-1150	Wall (Middle) - Rebar Fixing & Working Platform	4	0	12-Mar-17 A	12-Apr-17 A		Calendar Day																				
S9B-T5-B13-1160	Wall (Middle) - Formwork	2	0	13-Apr-17 A	14-Apr-17 A		Calendar Day																				
S9B-T5-B13-1170	Wall (Middle) - Concrete	1	0	15-Apr-17 A	15-Apr-17 A		Calendar Day																				
S9B-T5-B13-1180	Wall (Middle) - Curing & Formwork Dismantling	3	0	16-Apr-17 A	19-Apr-17 A		Calendar Day																				
S9B-T5-B13-1185	Construct Roadside Barriers	6	2	12-Apr-17 A	21-Apr-17	-549	Calendar Day																				
S9B-T5-B13-1230	OHVD Base Slab (North) - Scaffolding Erection	10	10	22-Apr-17	01-May-17	-549	Calendar Day																				
S9B-T5-B13-1240	OHVD Base Slab (North) - Formwork & Rebar Fixing	7	7	29-Apr-17	05-May-17	-546	Calendar Day																				
S9B-T5-B13-1250	OHVD Base Slab (North) - Concrete & Curing	2	2	06-May-17	07-May-17	-546	Calendar Day																				

◆ Milestone

◆ Critical Milestones

█ Current Works

█ Critical Works

█ Remaining Level of Effort

CHUN WO - CRGL
JOINT VENTURE

CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (dd 20-Apr-17)

Date

Revision

Checked

Approved

Rev. Programme (08-Apr-...

[illegible]

[illegible]

[illegible]

- ◆ Milestone
- ◆ Critical Milestones
- Current Works
- Critical Works
- Remaining Level of Effort

CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (dd 20-Apr-17)

[illegible]

- ◆ Milestone
- ◆ Critical Milestones
- Current Works
- Critical Works
- Remaining Level of Effort

CEDD CONTRACT NO. HK/2009/02
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (dd 20-Apr-17)

[illegible]

[illegible]

[illegible][illegible]

[illegible]

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2	2017			
								Jan	Feb	Mar	Apr
HK/2012/08 Revised Works Programme Rev.9(DD 31 December 2016)											
Dredging and Reclamation											
Marine Work Construction											
Others - Landing Steps											
MAR21420	Zone A2 - [summary] landing steps at seawall 13	73	09-Feb-17	11-May-17	-23	0%					
MAR21360	Zone A2 - [summary] landing steps at seawall 4	77	09-Feb-17	16-May-17	-27	0%					
MAR21380	Zone B - [summary] landing steps at seawall 5	73	09-Feb-17	11-May-17	-23	0%					
MAR21400	Zone D - [summary] landing steps at seawall 9	70	09-Feb-17	08-May-17	-20	0%					
Works for Section Completion											
Construction											
Section II - MVB Structure											
MVB Substructure - ELS & Structural Works for Portion A											
MVB Substructure - Other Works for Portion A											
SII11400	Sec II - MVB A: Backfilling to ground level (2.0mPD to 4.0mPD)	14	17-Jan-17	30-Jan-17	-163	0%					
SII11320	Sec II - MVB A: Remove flamework & formwork	10	05-Jan-17	14-Jan-17	-143	0%					
SII11340	Sec II - MVB A: Repair defect	10	15-Jan-17	24-Jan-17	-143	0%					
SII11360	Sec II - MVB A: Screeding of Roof Slab	7	10-Jan-17	16-Jan-17	-163	0%					
SII11344	Sec II - MVB A: Waterproofing of D-wall	5	25-Jan-17	29-Jan-17	-143	0%					
SII11350	Sec II - MVB A: Waterproofing of Roof Slab	7	10-Jan-17	16-Jan-17	-163	0%					
MVB Substructure - ELS & Structural Works for Portion B											
MVB Substructure - Structural Works for Portion B											
SII12450	Sec II - MVB B - Construct remaining walland slab below B1/F	11	31-Dec-16*	10-Jan-17	-255	0%					
SII12560	Sec II - MVB B: Constrcut wall above capping beam and slab at G/F	28	19-Jan-17	15-Feb-17	-160	0%					
SII12520	Sec II - MVB B: Construct Capping Beam at South	19	31-Dec-16	18-Jan-17	-160	0%					
SII12500	Sec II - MVB B: Construct wall of B1/F and capping beam at East	15	31-Dec-16	14-Jan-17	-259	0%					
MVB Substructure - Other Works for Portion B											
SII12360	Sec II - MVB B: Repair Defect	10	25-Jan-17	03-Feb-17	-154	0%					
SII12120	Sec II - MVB B: seal up the openings	5	25-Jan-17	29-Jan-17	-143	0%					
SII12420	Sec II - MVB B: Waterproofing of D-wall	6	04-Feb-17	09-Feb-17	-154	0%					
SII12100	Sec III - MVB B: Remove falsework & formwork	10	15-Jan-17	24-Jan-17	-154	0%					
MVB Substructure - ELS & Structural Works for Portion C											
MVB Substructure - ELS for Portion C											
SII12380	Sec III - MVB C : Remove bulhead wall between MVB plant room and MVB South	7	21-Dec-16 A	06-Jan-17	-185	56.25%					
MVB Substructure - Structural Works for Portion C											
SII12600	Sec II - MVB Plant Room : Construct fence wall above G/F slab	14	25-Feb-17	10-Mar-17	-192	0%					



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2	2017			
								Jan	Feb	Mar	Apr
SII12260	Sec II - MVB Plant Room : Construct Floor Slab of G/F	11	14-Jan-17	24-Jan-17	-192	0%					
SII12580	Sec II - MVB Plant Room : Construct slab of Raised Floor	15	10-Feb-17	24-Feb-17	-192	0%					
SII12240	Sec II - MVB Plant Room : Construct Wall of B1/F	14	22-Dec-16 A	13-Jan-17	-192	15%					
SII12540	Sec II - MVB Plant Room : Construct wall of Raised Floor	16	25-Jan-17	09-Feb-17	-192	0%					
Section II A - CWB Tunnel & Slip Road Structures and Facilities											
CWB A2(2)											
CWB A2 (2) - ELS & Tunnel Structure											
CWB A2 - Other Works											
SIIA12660	Sec II A - CWB A2(2) : Backfilling from +2.0mPD to formation level	25	07-Feb-17	03-Mar-17	-229	0%					
SIIA12610	Sec II A - CWB A2(2) : Backfilling up to +2.0 mPD	14	25-Nov-16 A	13-Jan-17	-229	0%					
SIIA12630	Sec II A - CWB A2(2) : Demolition of temporary Dwall	24	14-Jan-17	06-Feb-17	-229	0%					
CWB B & A2(1)											
CWB B - ELS & Tunnel Structure											
CWB A2(1) & B - Tunnel Structure											
SIIA13900	Sec II A - CWB B: Construct Bay 7b - OHVD	15	13-Jan-17	27-Jan-17	-257	0%					
SIIA13920	Sec II A - CWB B: Construct Bay 7b - Top Slab	14	02-Feb-17	15-Feb-17	-257	0%					
SIIA13880	Sec II A - CWB B: Construct Bay 7b - Wall	19	19-Dec-16 A	18-Jan-17	-257	38.71%					
CWB A2(1) & B - Associated Facilities											
SIIA14460	Sec II A - CWB A2(1) & B : Civil Provisions - waterproofing & lay screeding	14	19-Feb-17	04-Mar-17	-231	0%					
SIIA14480	Sec II A - CWB A2(1) & B : Remove flasework & formwork	7	16-Feb-17	22-Feb-17	-257	0%					
SIIA14500	Sec II A - CWB A2(1) & B : Repair defect	7	23-Feb-17	02-Mar-17	-209	0%					
CWB C (W)											
CWB C(W) - ELS & Tunnel Structure											
CWB C(W) - Tunnel Structure											
SIIA12650	Sec II A - CWB CW: Construct Bay 1 & 2 - Internal Wall	8	09-Jan-17	16-Jan-17	-258	0%					
SIIA12700	Sec II A - CWB CW: Construct Bay 1 & 2 - OHVD	11	17-Jan-17	27-Jan-17	-258	0%					
SIIA12720	Sec II A - CWB CW: Construct Bay 1 & 2 - Roof Slab	23	03-Feb-17	25-Feb-17	-258	0%					
SIIA12640	Sec II A - CWB CW: Construct Bay 1 & 2 - Southern Wall	8	09-Jan-17	16-Jan-17	-257	0%					
SIIA12460	Sec II A - CWB CW: Construct Bay 2b - B1/F slab	14	23-Jan-17	05-Feb-17	-111	0%					
SIIA12520	Sec II A - CWB CW: Construct Bay 2b - G/F roof slab	7	13-Feb-17	19-Feb-17	-118	0%					
SIIA12430	Sec II A - CWB CW: Construct Bay 2b - Saw cut D-wall at B1/F	14	09-Jan-17	22-Jan-17	-118	0%					
SIIA12480	Sec II A - CWB CW: Construct Bay 2b - Saw cut D-wall at G/F	21	23-Jan-17	12-Feb-17	-118	0%					
SIIA12180	Sec II A - CWB CW: Construct Raking Struts	4	23-Dec-16 A	03-Jan-17	-258	50%					
SIIA12200	Sec II A - CWB CW: Remove walling/strut/comcrete packing	5	04-Jan-17	08-Jan-17	-258	0%					
CWB C(W) - Associated Facilities											
SIIA14220	Sec II A - CWB CW: Remove flasework & formwork	7	26-Feb-17	04-Mar-17	-258	0%					
SIIA14240	Ssec II A - CWB CW: Repair defect	7	26-Feb-17	04-Mar-17	-258	0%					
CWB C (E)											
CWB C(E) - ELS & Tunnel Structure											
CWB C(E) - Tunnel Structure											

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2	2017			
								Jan	Feb	Mar	Apr
SIIA13455	Sec II A - CWB CE: Construct Bay 3 - Roof Slab	11	17-Jan-17	27-Jan-17	-240	0%					
SIIA13444	Sec II A - CWB CE: Remove concrete wall between C1 and zone CE (Bay 3)	6	11-Jan-17*	16-Jan-17	-240	0%					
CWB C(E) - Other Works											
SIIA13325	Sec II A - CWB CE: backfill to +4.0mPD	45	11-Feb-17	27-Mar-17	-154	0%					
SIIA13300	Sec II A - CWB CE: Remove flasework and formwork	8	28-Jan-17	04-Feb-17	-240	0%					
SIIA13310	Sec IIA - CWB CE: Repair defect	8	06-Feb-17	14-Feb-17	-195	0%					
SIIA13316	Ssec IIA - CWB CE: Waterproofing of D-wall	5	15-Feb-17	20-Feb-17	-195	0%					
CWB C(E) - Associated Facilities											
SIIA14272	Sec II A - CWB CE: Civil Provisions - lay screeding and waterproofing	14	28-Jan-17	10-Feb-17	-154	0%					
CWB C - Exhaust Duct											
CWB C - Exhaust Duct Structural Work											
SIIA12936	Sec II A - Exhaust Duct at Slip Rd 3: Demolish bulkhead between MVB south and exhaust duct	18	15-Jan-17	01-Feb-17	-259	0%					
SIIA12938	Sec II A - Exhaust Duct at Slip Rd3: Construt Bay 1 - base slab	8	02-Feb-17	09-Feb-17	-259	0%					
SIIA13480	Sec II A - Exhaust Duct at Slip Rd3: Construt Bay 1 - roof slab	8	19-Feb-17	26-Feb-17	-259	0%					
SIIA12940	Sec II A - Exhaust Duct at Slip Rd3: Construt Bay 1 - wall	9	10-Feb-17	18-Feb-17	-259	0%					
CWB C - Exhaust Duct Others											
SIIA12950	Sec II A - Exhaust Duct at Slip Rd3: dismantle formwork / falsework	12	27-Feb-17	10-Mar-17	-259	0%					
CWB D - Slip Road 1											
CWB D - Slip Road 1 - ELS & Tunnel Structure											
CWB D - Slip Road 1 - ELS											
CWB D - SR1 - ELS - Bay 1 & 2											
SIIA 12584	Sec II A - CWB SR1 Concrete Plug: Remove concrete bulkhead	14	02-Feb-17	15-Feb-17	-249	0%					
CWB D - Slip Road 1 - Tunnel Structure											
SIIA13060	Sec II A - CWB SR1: Construct Bay 1a - Base Slab (adjacent to C4 unit)	17	11-Jan-17	27-Jan-17	-249	0%					
SIIA13080	Sec II A - CWB SR1: Construct Bay 1a - Roof Slab (adjacen to C4 unit)	13	16-Feb-17	28-Feb-17	-249	0%					
SIIA13055	Sec II A - CWB SR1: Trimming and post drill to Bay 1a base slab	11	31-Dec-16	10-Jan-17	-249	0%					
CWB D - Associated Facilities											
SIIA13940	Sec II A - CWB SR1 : Repair Defect	7	08-Jan-17	14-Jan-17	-209	0%					
SIIA13980	Sec II A - CWB SR1 : Waterproofing of D-wall	5	15-Jan-17	19-Jan-17	-209	0%					
SIIA12580	Sec II A - CWB SR1: Civil Provisions - Waterproofing & lay screeding	14	09-Jan-17	22-Jan-17	-212	0%					
SIIA13560	Sec II A - CWB SR1: Remove falsework and formwork	7	01-Jan-17	07-Jan-17	-209	0%					
CWB D - Slip Road 1 - Trough / Retaining Wall											
CWB D - Slip Road 1 - Trough/Retaining Wall Temp Work & ELS											
SIIA13320	Sec II A - CWB SR1 Trough & RW: Remedial works for Blinding layer (Trough Bay 1)	10	10-Jan-17	19-Jan-17	-271	0%					
SIIA13780	Sec II A - CWB SR1 Trough & RW: Remedial works for Blinding layer (Trough Bay 2)	5	05-Jan-17	09-Jan-17	-271	0%					
SIIA14000	Sec II A - CWB SR1 Trough & RW: Remedial works for Blinding layer (Trough Bay 3)	5	14-Dec-16 A	04-Jan-17	-271	75%					
SIIA14080	Sec II A - CWB SR1 Trough & RW: Retaining Wall - Cast Blinding Layer	2	15-Jan-17	16-Jan-17	-263	0%					
SIIA14060	Sec II A - CWB SR1 Trough & RW: Retaining Wall - Excavation	7	08-Jan-17*	14-Jan-17	-263	0%					
CWB D - Slip Road 1 - Trough/Retaining Wall Structure											
SIIA13800	Sec II A - CWB SR1 Trough & RW: Retaining Walls RW3 (bay 1)	19	17-Jan-17	04-Feb-17	-263	0%					

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2	2017			
								Jan	Feb	Mar	Apr
SIIA13820	Sec II A - CWB SR1 Trough & RW: Retaining Walls RW3 (bay 2&3)	18	25-Jan-17	11-Feb-17	-263	0%					
SIIA13860	Sec II A - CWB SR1 Trough & RW: Retaining Walls RW4 (bay 1)	19	17-Jan-17	04-Feb-17	-256	0%					
SIIA12800	Sec II A - CWB SR1 Trough & RW: Trough Structure - Base Slab & Wall (bay 1)	31	20-Jan-17	19-Feb-17	-271	0%					
SIIA13740	Sec II A - CWB SR1 Trough & RW: Trough Structure - Base Slab & Wall (bay 3)	19	05-Jan-17	23-Jan-17	-244	0%					
SIIA13720	Sec II A - CWB SR1 Trough & RW: Trough Structure -Base Slab & Wall (bay 2)	31	10-Jan-17	09-Feb-17	-261	0%					
CWB D - Slip Road 1 - Trough/ Retaining Wall Other Works											
SIIA13845	Sec II A - CWB SR1: Waterproofing & lay screeding	14	20-Feb-17	05-Mar-17	-271	0%					
Section III A - Road A2, A4, A5, Area 11; Implement 2nd Stage ITA											
Roadwork & Utilities at CRIII/ A1											
SIIIA10260	Sec III A - roadwork and utilities (Zone A1) - Backfill to pavement founding level	42	06-Jan-17	28-Feb-17	-188	0%					
Roadwork & Utilities at B											
SIIIA10840	Sec III A - roadwork and utilities (Zone B) - Backfill to pavement founding level	40	28-Feb-17	19-Apr-17	-188	0%					
Box Culvert L1 & FRP-L - Bay 8											
Box Culvert L1 & FRP-L - Bay 8 Structure											
CUL11323	Culvert L - Bay 8 - construct base slab (Portion 1)	14	31-Dec-16	13-Jan-17	-259	0%					
CUL11324	Culvert L - Bay 8 - construct base slab (Portion 2)	9	14-Jan-17	22-Jan-17	-259	0%					
CUL11326	Culvert L - Bay 8 - construct wall	14	23-Jan-17	05-Feb-17	-259	0%					
CUL11328	Culvert L - bay 8 - construt top slab	11	17-Feb-17	27-Feb-17	-259	0%					
CUL11327	Culvert L - Bay 8 - Dismantle formwork & Remove sheet pipe	11	06-Feb-17	16-Feb-17	-259	0%					
Box Culvert L1 & FRP-L - Bay 8 Others											
CUL11340	Culvert L - bay 8 - backfill above box section	12	28-Feb-17	13-Mar-17	-211	0%					
Section VI D - Area 8B & 10											
WDII Box 1 Construction											
WDII Box 1 Remaining Structure											
WD-C6090	Sec VID - Remaining of Box I: Blasting tank at wall 12, 15 & 16	23	02-Feb-17	28-Feb-17	-237	0%					
WD-C6040	Sec VID - Remaining of Box I: Construct lower part BHW, Wall 12, 15 and 16	10	12-Dec-16 A	09-Jan-17	-290	62.96%					
WD-C6060	Sec VID - Remaining of Box I: Construct Upper part BHW, Wall 12, 15 and 16	17	10-Jan-17	26-Jan-17	-290	0%					
WD-C6080	Sec VID - Remaining of Box I: Construct Wall 13(23m run)	37	10-Jan-17	15-Feb-17	-278	0%					
WD-C6075	Sec VID -Remaining of Box I: Extension of sacarfical wall (2.3m)	37	27-Jan-17	04-Mar-17	-281	0%					
Section IV - Slip Road 3											
Roadwork & Utilities (Lung King Street)											
SIV11060	Sec IV - Stage 3: Roadwork & Utilities	23	11-Nov-16 A	27-Jan-17	-79	0%					
Section VII - Remainder Works											
Retaining Wall RW5 Construction											
SVII10660	Sec VII - Retaining Wall RW5 (bay 1) - construct base slab and wall	18	03-Feb-17*	23-Feb-17	-24	0%					
SVII10680	Sec VII - Retaining wall RW5 (bay 2) - construct base slab and wall	18	24-Feb-17	16-Mar-17	-24	0%					
SVII10800	Sec VII - Retaining wall RW5 (bay 3) - construct base slab and wall	18	03-Feb-17	23-Feb-17	-24	0%					
SVII10820	Sec VII - Retaining wall RW5 (bay 4) - construct base slab and wall	18	24-Feb-17	16-Mar-17	-24	0%					
Landing Steps Construction											
Landing Steps BSW13											

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2	2017			
								Jan	Feb	Mar	Apr
SVII10700	Sec VII - Landing steps (BSW13) - construct mass concrete coping	26	09-Feb-17*	10-Mar-17	-27	0%					
Landing Steps BSW4											
SVII10940	Sec VII - Landing steps (BSW4) - construct mass concrete coping	26	09-Feb-17	10-Mar-17	-27	0%					
Landing Steps BSW5											
SVII11020	Sec VII - Landing steps (BSW5) - construct mass concrete coping	26	09-Feb-17	10-Mar-17	-23	0%					
Landing Steps BSW9											
SVII11100	Sec VII - Landing steps (BSW9) - construct mass concrete coping	24	09-Feb-17*	08-Mar-17	-20	0%					
Promenade Seawall Parapet Construction											
SVII10400	Sec VII - construct block seawall mass concrete coping & backfill to pavement formation	60	06-Feb-17*	20-Apr-17	-12	0%					
Section VIII - Landscape Softworks											
Soft Landscaping Works											
SVIII10040	Sec VIII - Trees Planting	64	31-Dec-16	21-Mar-17	-57	0%					
Section X - Protection & Preservation of Trees											
Soft Landscaping Works											
SX10020	Sec X - Protection & Preservation of Trees	265	31-Jan-13 A	21-Sep-17	-52	83.76%					
VO : Construction of Box 4A & 4B											
Box 4A											
4A10000	Concrete Fill with 300 dia. carrier drain (Approx. 50m)	10	05-Jan-17*	14-Jan-17	-217	0%					
4A10020	Internal Suspended Slab & Internal Wall	13	15-Jan-17	27-Jan-17	-217	0%					
Box 4B											
4B10000	Concrete Fill with 300 dia. carrier drain (Approx. 50m)	10	05-Jan-17	14-Jan-17	-205	0%					
4B10010	Internal Suspended Slab & Internal Wall	13	15-Jan-17	27-Jan-17	-217	0%					



中國建築-利達聯營
CHINA STATE - LEADER JOINT VENTURE

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Page : 1 / 3

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	Apr	May	Jun	Jul	Aug
HK/2012/08 Works Programme Rev.10(DD 31 March 2017)											
Works for Section Completion											
Construction											
Section II A - CWB Tunnel & Slip Road Structures and Facilities											
CWB D - Slip Road 1 - Trough / Retaining Wall											
CWB D - Slip Road 1 - Trough/Retaining Wall Structure											
SIIA12788	Sec II A - CWB SR1 Trough & RW: jet grout for seepage at SR1 trough	27	11-Mar-17 A	26-Apr-17	48	0%					
SIIA12800	Sec II A - CWB SR1 Trough & RW: Trough Structure - Base Slab & Wall (bay 1)	15	23-May-17	06-Jun-17	59	0%					
SIIA13720	Sec II A - CWB SR1 Trough & RW: Trough Structure -Base Slab & Wall (bay 2)	15	08-May-17	22-May-17	48	0%					
SIIA13740	Sec II A - CWB SR1 Trough & RW: Trough Structure - Base Slab & Wall (bay 3)	15	14-May-17	28-May-17	48	0%					
SIIA13800	Sec II A - CWB SR1 Trough & RW: Retaining Walls RW3 & RW4 (bay 1)	16	29-May-17	13-Jun-17	48	0%					
SIIA13860	Sec II A - CWB SR1 Trough & RW: Retaining Walls RW3 & RW4 (bay 2)	15	03-Jun-17	17-Jun-17	48	0%					
Section III A - Road A2, A4 & A5											
Roadwork & Utilities - Section 1 (L1806 - L1801)											
SIIIA10280	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (TTA Stage 4A, 4B & 4C)	52	10-Apr-17*	15-Jun-17	15	0%					
SIIIA10290	Sec III A - roadwork and utilities section 1 carriageway - TTA Stage 5	15	26-Jun-17*	13-Jul-17	7	0%					
Roadwork & Utilities - Section 2 (L1810 - L1806)											
SIIIA12470	Sec III A - roadwork and utilities section 2 carriageway - Relocate site access	14	29-Jun-17*	15-Jul-17	8	0%					
Roadwork & Utilities - Section 4 (L1406 - L1401)											
SIIIA12930	Sec III A - roadwork and utilities section 4 carriageway - Drainage works (L1406 -L1401)	59	08-May-17*	17-Jul-17	0	0%					
Roadwork & Utilities - Section 5 (L1411 - L1406)											
SIIIA13150	Sec III A - roadwork and utilities section 5 carriageway - Drainage works (L1411 - L1406)	44	25-May-17*	17-Jul-17	0	0%					
Roadwork & Utilities - Section 6 (L1102 - L1411)											
SIIIA13370	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (Culvert L - L1411)	49	10-May-17*	07-Jul-17	14	0%					
Section V - Remaining At-Grade Road; Remove 2nd Stage ITA											
Roadwork & Utilities											
Section 1 (L1504 - L1900)											
SV12420	Sec V - Roadwork & Utilities Section 1 Carriageway - Drainage Works at MVB North	112	16-Mar-17 A	17-Aug-17	57	0%					
SV12450	Sec V - Roadwork & Utilities Section 1 Carriageway - Gully pipe	109	05-May-17	11-Sep-17	57	0%					
Section 2 (L1510 - L1504)											
SV12600	Sec V - Roadwork & Utilities Section 2 Carriageway - Drainage Works (L1501-L1507, L1406B-L1406A,	82	25-May-17*	30-Aug-17	0	0%					
Section 3 (Culvert L - L1504)											
SIV12760	Sec V - Roadwork & Utilities Section 3 Carriageway - Drainage Works (Culvert L - L1504 & L1406B - L1406C)	51	16-Mar-17 A	06-Jun-17	130	0%					
SIV12800	Sec V - Roadwork & Utilities Section 3 Carriageway - Gully pipe (Culvert L - L1504)	30	07-Jun-17	12-Jul-17	130	0%					
Box Culvert L1 & FRP-L - Bay 8											

Data Date:
31-Mar-17

- ◆ ◆ Current Milestone
- ■ Actual Work
- ■ Critical Remaining Work
- ■ Remaining Work
- ■ Remaining Level of Effort

Three Months Rolling Programme for Non-CRIII (Apr 2017 to Jun 2017)
(Ref. to Works Programme Rev.10)

Date	Revision	Checked	Approved
11-May-17			



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2017				
							Apr	May	Jun	Jul	Aug
Box Culvert L1 & FRP-L - Bay 8 Structure											
CUL11328	Culvert L - bay 8 - construt top slab	12	10-Apr-17*	21-Apr-17	79	0%					
Box Culvert L1 & FRP-L - Bay 8 Others											
CUL11340	Culvert L - bay 8 - backfill above box section	25	03-Jun-17*	03-Jul-17	30	0%					
Section VI D - Area 8B & 10											
WDII Box 1 Construction											
WDII Box 1 Remaining Structure											
WD-C6075	Sec VID -Remaining of Box I: Construct sacarfical wall (2.3m)	11	19-Mar-17 A	10-Apr-17	0	60.71%					
WD-C6080	Sec VID - Remaining of Box I: Construct Wall 13(23m run)	16	07-Mar-17 A	15-Apr-17	8	46.67%					
WD-C6090	Sec VID - Remaining of Box I:Construct 2.5m wall 13	13	11-Apr-17	23-Apr-17	0	0%					
WD-C6120	Sec VID - Remaining of Box I: Blasting and final sink box to -10.0 mPD	2	24-Apr-17	25-Apr-17	0	0%					
WD-C6122	Sec VID - Remaining of Box I: Stiching of 4 bored piles	12	26-Apr-17	07-May-17	0	0%					
WD-C6124	Sec VID - Remaining of Box I: Scaffoding and soffit work at 4 bored piles	10	08-May-17	17-May-17	0	0%					
WD-C6126	Sec VID - Remaining of Box I: Roof rebar and concreting flat roof	8	18-May-17	25-May-17	0	0%					
WD-C6128	Sec VID - Remaining of Box I: Construct remaining roof half joint	7	28-May-17	03-Jun-17	0	0%					
WD-C6130	Sec VID - Remaining of Box I: Waterproofing work of roof	12	04-Jun-17	15-Jun-17	0	0%					
WD-C6140	Sec VID - Backfilling at South of Box I : Backfilling bagged cement to -6.5mPD	5	26-Apr-17	30-Apr-17	6	0%					
WD-C6160	Sec VID - Backfilling at South of Box I : Remove all ELS shoring and cut off P7 to P58 at -6.5mPD	18	01-May-17	18-May-17	6	0%					
WD-C6200	Sec VID - Backfilling at South of Box I : Remove SIC coarse screen hood	11	19-May-17	29-May-17	6	0%					
WD-C6220	Sec VID - Backfilling at South of Box I : Install pipe cap for box beam	4	30-May-17	02-Jun-17	6	0%					
WD-C6222	Sec VID - Backfilling at South of Box I : Stiching of H-pile	4	03-Jun-17	06-Jun-17	6	0%					
WD-C6223	Sec VID - Backfilling at South of Box I : Bagged lighweight concrete btw cap & seawall	6	07-Jun-17	12-Jun-17	6	0%					
WD-C6240	Sec VID - Backfilling at South of Box I : Install box beam	4	13-Jun-17	16-Jun-17	6	0%					
WD-C6250	Sec VID - Backfilling at South of Box I : Place 400mm thk precast cover to SIC	4	17-Jun-17	20-Jun-17	6	0%					
WD-C6255	Sec VID - Backfilling at South of Box I : Bagged lightweight concrete btw precast cover and box beam	4	21-Jun-17	24-Jun-17	6	0%					
WD-C6275	Sec VID - Backfilling at North of Box I : Type C concrete block at Box I half joint	4	19-May-17	22-May-17	13	0%					
WD-C6295	Sec VID - Backfilling at North of Box I : Install ceramsite concrete blocks	8	23-May-17	30-May-17	13	0%					
WD-C6315	Sec VID - Backfilling at North of Box I : Type A concrete block at roof of Box 1/2	3	31-May-17	02-Jun-17	13	0%					
WD-C6320	Sec VI D - Public fill on the top of Box I	15	16-Jun-17	30-Jun-17	0	0%					
Section IV - Slip Road 3											
Roadwork & Utilities											
Section 2 (L2301 - L2103)											
SIV11940	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works	35	20-Apr-17*	02-Jun-17	0	0%					
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Watermain	10	28-Jun-17	10-Jul-17	161	0%					
SIV12000	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe	21	03-Jun-17	27-Jun-17	161	0%					
Section VII - Remainder Works											
Promenade Seawall Parapet Construction											
SVII10400	Sec VII - construct block seawall mass concrete coping & backfill to pavement formation	50	15-Jun-17*	12-Aug-17	13	0%					
Section VIII - Landscape Softworks											
Soft Landscaping Works											



中國建築-利達聯營
CHINA STATE - LEADER JOINT VENTURE

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2017				
							Apr	May	Jun	Jul	Aug
SVIII10040	Sec VIII - Trees Planting	118	31-Mar-17	24-Aug-17	0	0%					
Section X - Protection & Preservation of Trees											
Soft Landscaping Works											
SX10020	Sec X - Protection & Preservation of Trees	234	31-Jan-13 A	19-Nov-17	0	85.66%					



中國建築-利達聯營
CHINA STATE - LEADER JOINT VENTURE

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Page : 1 / 3

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	Apr	May	Jun	Jul	Aug
HK/2012/08 Works Programme Rev.10(DD 31 March 2017)											
Works for Section Completion											
Construction											
Section II A - CWB Tunnel & Slip Road Structures and Facilities											
CWB D - Slip Road 1 - Trough / Retaining Wall											
CWB D - Slip Road 1 - Trough/Retaining Wall Structure											
SIIA12788	Sec II A - CWB SR1 Trough & RW: jet grout for seepage at SR1 trough	27	11-Mar-17 A	26-Apr-17	48	0%					
SIIA12800	Sec II A - CWB SR1 Trough & RW: Trough Structure - Base Slab & Wall (bay 1)	15	23-May-17	06-Jun-17	59	0%					
SIIA13720	Sec II A - CWB SR1 Trough & RW: Trough Structure -Base Slab & Wall (bay 2)	15	08-May-17	22-May-17	48	0%					
SIIA13740	Sec II A - CWB SR1 Trough & RW: Trough Structure - Base Slab & Wall (bay 3)	15	14-May-17	28-May-17	48	0%					
SIIA13800	Sec II A - CWB SR1 Trough & RW: Retaining Walls RW3 & RW4 (bay 1)	16	29-May-17	13-Jun-17	48	0%					
SIIA13860	Sec II A - CWB SR1 Trough & RW: Retaining Walls RW3 & RW4 (bay 2)	15	03-Jun-17	17-Jun-17	48	0%					
Section III A - Road A2, A4 & A5											
Roadwork & Utilities - Section 1 (L1806 - L1801)											
SIIIA10280	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (TTA Stage 4A, 4B & 4C)	52	10-Apr-17*	15-Jun-17	15	0%					
SIIIA10290	Sec III A - roadwork and utilities section 1 carriageway - TTA Stage 5	15	26-Jun-17*	13-Jul-17	7	0%					
Roadwork & Utilities - Section 2 (L1810 - L1806)											
SIIIA12470	Sec III A - roadwork and utilities section 2 carriageway - Relocate site access	14	29-Jun-17*	15-Jul-17	8	0%					
Roadwork & Utilities - Section 4 (L1406 - L1401)											
SIIIA12930	Sec III A - roadwork and utilities section 4 carriageway - Drainage works (L1406 -L1401)	59	08-May-17*	17-Jul-17	0	0%					
Roadwork & Utilities - Section 5 (L1411 - L1406)											
SIIIA13150	Sec III A - roadwork and utilities section 5 carriageway - Drainage works (L1411 - L1406)	44	25-May-17*	17-Jul-17	0	0%					
Roadwork & Utilities - Section 6 (L1102 - L1411)											
SIIIA13370	Sec III A - roadwork and utilities section 1 carriageway - Drainage works (Culvert L - L1411)	49	10-May-17*	07-Jul-17	14	0%					
Section V - Remaining At-Grade Road; Remove 2nd Stage ITA											
Roadwork & Utilities											
Section 1 (L1504 - L1900)											
SV12420	Sec V - Roadwork & Utilities Section 1 Carriageway - Drainage Works at MVB North	112	16-Mar-17 A	17-Aug-17	57	0%					
SV12450	Sec V - Roadwork & Utilities Section 1 Carriageway - Gully pipe	109	05-May-17	11-Sep-17	57	0%					
Section 2 (L1510 - L1504)											
SV12600	Sec V - Roadwork & Utilities Section 2 Carriageway - Drainage Works (L1501-L1507, L1406B-L1406A,	82	25-May-17*	30-Aug-17	0	0%					
Section 3 (Culvert L - L1504)											
SIV12760	Sec V - Roadwork & Utilities Section 3 Carriageway - Drainage Works (Culvert L - L1504 & L1406B - L1406C)	51	16-Mar-17 A	06-Jun-17	130	0%					
SIV12800	Sec V - Roadwork & Utilities Section 3 Carriageway - Gully pipe (Culvert L - L1504)	30	07-Jun-17	12-Jul-17	130	0%					
Box Culvert L1 & FRP-L - Bay 8											

Data Date:
31-Mar-17

- ◆ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

Three Months Rolling Programme for Non-CRIII (Apr 2017 to Jun 2017)
(Ref. to Works Programme Rev.10)

Date	Revision	Checked	Approved
11-May-17			



Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2017				
							Apr	May	Jun	Jul	Aug
Box Culvert L1 & FRP-L - Bay 8 Structure											
CUL11328	Culvert L - bay 8 - construt top slab	12	10-Apr-17*	21-Apr-17	79	0%					
Box Culvert L1 & FRP-L - Bay 8 Others											
CUL11340	Culvert L - bay 8 - backfill above box section	25	03-Jun-17*	03-Jul-17	30	0%					
Section VI D - Area 8B & 10											
WDII Box 1 Construction											
WDII Box 1 Remaining Structure											
WD-C6075	Sec VID -Remaining of Box I: Construct sacarfical wall (2.3m)	11	19-Mar-17 A	10-Apr-17	0	60.71%					
WD-C6080	Sec VID - Remaining of Box I: Construct Wall 13(23m run)	16	07-Mar-17 A	15-Apr-17	8	46.67%					
WD-C6090	Sec VID - Remaining of Box I:Construct 2.5m wall 13	13	11-Apr-17	23-Apr-17	0	0%					
WD-C6120	Sec VID - Remaining of Box I: Blasting and final sink box to -10.0 mPD	2	24-Apr-17	25-Apr-17	0	0%					
WD-C6122	Sec VID - Remaining of Box I: Stiching of 4 bored piles	12	26-Apr-17	07-May-17	0	0%					
WD-C6124	Sec VID - Remaining of Box I: Scaffoding and soffit work at 4 bored piles	10	08-May-17	17-May-17	0	0%					
WD-C6126	Sec VID - Remaining of Box I: Roof rebar and concreting flat roof	8	18-May-17	25-May-17	0	0%					
WD-C6128	Sec VID - Remaining of Box I: Construct remaining roof half joint	7	28-May-17	03-Jun-17	0	0%					
WD-C6130	Sec VID - Remaining of Box I: Waterproofing work of roof	12	04-Jun-17	15-Jun-17	0	0%					
WD-C6140	Sec VID - Backfilling at South of Box I : Backfilling bagged cement to -6.5mPD	5	26-Apr-17	30-Apr-17	6	0%					
WD-C6160	Sec VID - Backfilling at South of Box I : Remove all ELS shoring and cut off P7 to P58 at -6.5mPD	18	01-May-17	18-May-17	6	0%					
WD-C6200	Sec VID - Backfilling at South of Box I : Remove SIC coarse screen hood	11	19-May-17	29-May-17	6	0%					
WD-C6220	Sec VID - Backfilling at South of Box I : Install pipe cap for box beam	4	30-May-17	02-Jun-17	6	0%					
WD-C6222	Sec VID - Backfilling at South of Box I : Stiching of H-pile	4	03-Jun-17	06-Jun-17	6	0%					
WD-C6223	Sec VID - Backfilling at South of Box I : Bagged lighweight concrete btw cap & seawall	6	07-Jun-17	12-Jun-17	6	0%					
WD-C6240	Sec VID - Backfilling at South of Box I : Install box beam	4	13-Jun-17	16-Jun-17	6	0%					
WD-C6250	Sec VID - Backfilling at South of Box I : Place 400mm thk precast cover to SIC	4	17-Jun-17	20-Jun-17	6	0%					
WD-C6255	Sec VID - Backfilling at South of Box I : Bagged lightweight concrete btw precast cover and box beam	4	21-Jun-17	24-Jun-17	6	0%					
WD-C6275	Sec VID - Backfilling at North of Box I : Type C concrete block at Box I half joint	4	19-May-17	22-May-17	13	0%					
WD-C6295	Sec VID - Backfilling at North of Box I : Install ceramsite concrete blocks	8	23-May-17	30-May-17	13	0%					
WD-C6315	Sec VID - Backfilling at North of Box I : Type A concrete block at roof of Box 1/2	3	31-May-17	02-Jun-17	13	0%					
WD-C6320	Sec VI D - Public fill on the top of Box I	15	16-Jun-17	30-Jun-17	0	0%					
Section IV - Slip Road 3											
Roadwork & Utilities											
Section 2 (L2301 - L2103)											
SIV11940	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Drainage Works	35	20-Apr-17*	02-Jun-17	0	0%					
SIV11960	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Watermain	10	28-Jun-17	10-Jul-17	161	0%					
SIV12000	Sec IV - Roadwork & Utilities at SR3 Section 2 Carriageway - Gully pipe	21	03-Jun-17	27-Jun-17	161	0%					
Section VII - Remainder Works											
Promenade Seawall Parapet Construction											
SVII10400	Sec VII - construct block seawall mass concrete coping & backfill to pavement formation	50	15-Jun-17*	12-Aug-17	13	0%					
Section VIII - Landscape Softworks											
Soft Landscaping Works											



中國建築-利達聯營
CHINA STATE - LEADER JOINT VENTURE

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central - Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Total Float	Activity % Complete	2017				
							Apr	May	Jun	Jul	Aug
SVIII10040	Sec VIII - Trees Planting	118	31-Mar-17	24-Aug-17	0	0%					
Section X - Protection & Preservation of Trees											
Soft Landscaping Works											
SX10020	Sec X - Protection & Preservation of Trees	234	31-Jan-13 A	19-Nov-17	0	85.66%					

SR8_DWP_R07-MU45		SR8 - Layout for 3MRP_2106_12			Appendix C.5													
Activity ID		Activity Name		Original Duration	Start	Finish												
							2016		2017									
							Dec	Jan			Feb			Mar			Apr	
Total				1791d	21-Mar-13 A	14-Dec-17												
DWP-07 (5) - Update Progress As of 20 Dec 16				1791d	21-Mar-13 A	14-Dec-17												
Works in KD7				137d	03-Oct-16 A	24-Mar-17												
Works in TS3-West				137d	03-Oct-16 A	24-Mar-17												
Tunnel Structure				137d	03-Oct-16 A	24-Mar-17												
TS3W CCT Structure (Mainline E/B, W/B Tunnel)				60d	03-Oct-16 A	14-Jan-17												
Wall & CP of Tunnel Structure Northern & Southem Tunnel E/B & W/B - 4,000 m3 + SM(A), SM(B), TF(A)				22d	21-Nov-16 A	22-Dec-16 A												
Bay 2				5d	25-Nov-16 A	06-Dec-16 A												
A1500	Spray Type Waterproofing, Protection Board and Backfilling (EP02 Construction Controlled)			5d	25-Nov-16 A	06-Dec-16 A	erproofing, Protection Board and Backfilling (EP02 Construction Controlled)											
Bay 3				10d	25-Nov-16 A	04-Dec-16 A												
A1530	Spray Type Waterproofing, Protection Board and Backfilling			10d	25-Nov-16 A	04-Dec-16 A	oofing, Protection Board and Backfilling											
Bay 4				10d	21-Nov-16 A	09-Dec-16 A												
A1560	Spray Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction			10d	21-Nov-16 A	09-Dec-16 A	e Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction											
Bay 5				10d	08-Dec-16 A	09-Dec-16 A												
A1590	Spray Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction			10d	08-Dec-16 A	09-Dec-16 A	e Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction											
Bay 6				10d	09-Dec-16 A	12-Dec-16 A												
A1620	Spray Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction (EP03 Construction controlled)			10d	09-Dec-16 A	12-Dec-16 A	ay Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction (EP03 Construction controlled)											
Bay 7				10d	11-Dec-16 A	12-Dec-16 A												
A1650	Spray Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction			10d	11-Dec-16 A	12-Dec-16 A	ay Type Waterproofing, Protection Board and Backfilling for SR8 Tunnel Construction											
Bay 8				14d	30-Nov-16 A	22-Dec-16 A												
A1690	Removal of 6th and 7th layer ELS			14d	30-Nov-16 A	08-Dec-16 A	6th and 7th layer ELS											
A1720	Backfilling for construction of SR8B			6d	11-Dec-16 A	18-Dec-16 A	Backfilling for construction of SR8B											
A1680	Waterproofing and repropping installation			5d	19-Dec-16 A	22-Dec-16 A	Waterproofing and repropping installation											
OHVD, Maintenance Walkway & Profile Barrier Construction (Northern & Southern Tunnel E/B & W/B				27d	08-Dec-16 A	06-Jan-17												
Bay 8				27d	08-Dec-16 A	06-Jan-17												
A1880	Bay S8 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier			8d	08-Dec-16 A	19-Dec-16 A	Bay S8 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier											
A1870	Bay N8 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier			8d	30-Dec-16	06-Jan-17	Bay N8 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier											
Bay 9				21d	12-Dec-16 A	03-Jan-17												
A1900	Bay S9 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier			5d	12-Dec-16 A	21-Dec-16 A	Bay S9 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier											
A1890	Bay N9 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier			5d	30-Dec-16	03-Jan-17	Bay N9 OHVD and Kicker Wall, Maintenance Walkway and Profile Barrier											
Top Slab (Northern and Southern Side Tunnel E/B and W/B - 18000 m3)				47d	03-Oct-16 A	14-Jan-17												
Bay 1				30d	08-Nov-16 A	14-Jan-17												
A2090	Bulkhead Breakthrough of TS3E/TS3W			30d	08-Nov-16 A	14-Jan-17	Bulkhead Breakthrough of TS3E/TS3W											
Bay 6				11d	03-Oct-16 A	03-Dec-16 A												
A2020	Bay S6R Top Slab (29m approx.)			11d	03-Oct-16 A	30-Nov-16 A	rox.)											
A2010	Bay N6R Top Slab (27m approx.)			11d	05-Oct-16 A	03-Dec-16 A	m approx.)											
Bay 7				17d	31-Oct-16 A	09-Dec-16 A												
A2040	Bay S7R Top Slab (29m approx.)			10d	31-Oct-16 A	07-Dec-16 A	p Slab (29m approx.)											
A2030	Bay N7R Top Slab (26m approx.)			10d	07-Nov-16 A	09-Dec-16 A	Top Slab (26m approx.)											
Bay 8				6d	12-Dec-16 A	12-Jan-17												
A2060	Bay S8R Top Slab (29m approx.)			5d	12-Dec-16 A	03-Jan-17	Bay S8R Top Slab (29m approx.)											
A2050	Bay N8R Top Slab (26m approx.)			6d	22-Dec-16 A	12-Jan-17	Bay N8R Top Slab (26m approx.)											
Bay 9				1d	08-Dec-16 A	04-Jan-17												

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan		Feb			Mar			Apr
A2080	Bay S9R Top Slab (29m approx.)	1d	08-Dec-16 A	30-Dec-16				■ Bay S9R Top Slab (29m approx.)								
A2070	Bay N9R Top Slab (26m approx.)	1d	17-Dec-16 A	04-Jan-17				■ Bay N9R Top Slab (26m approx.)								
SR8 Tunnel Structure		96d	13-Nov-16 A	16-Feb-17												
Base Slab of Slip Road 8 (SR8) - 8000 m3		73d	13-Nov-16 A	24-Jan-17												
A2130	Placement of Seawall Blocks for SR4B Construction	8d	13-Nov-16 A	30-Dec-16				■ Placement of Seawall Blocks for SR4B Construction								
A2150	Placement of Seawall Blocks for SR5B Construction	8d	18-Nov-16 A	01-Jan-17				■ Placement of Seawall Blocks for SR5B Construction								
A2170	Placement of Seawall Blocks for SR6B Construction	8d	16-Dec-16 A	02-Jan-17				■ Placement of Seawall Blocks for SR6B Construction								
A2200	Bay SR8B	8d	30-Dec-16	06-Jan-17				■ Bay SR8B								
A2140	Bay SR4B	7d	31-Dec-16	06-Jan-17				■ Bay SR4B								
A2160	Bay SR5B	7d	01-Jan-17	08-Jan-17				■ Bay SR5B								
A2180	Bay SR6B	5d	02-Jan-17	07-Jan-17				■ Bay SR6B								
A2190	Bay SR7B	5d	11-Jan-17	15-Jan-17				■ Bay SR7B								
A2110	Breaking to the Cut Off Level of Diaphragm Wall to be Carried Out after Bay S3R Completion	2d	18-Jan-17	19-Jan-17				■ Breaking to the Cut Off Level of Diaphragm Wall to be Carried Out after Bay S3R Completion								
A2120	Bay SR3B	5d	20-Jan-17	24-Jan-17				■ Bay SR3B								
Wall Structure of SR8 - 2500 m3		27d	07-Jan-17	02-Feb-17												
A2230	Removal of 4th layer and 5th layer ELS	6d	07-Jan-17	12-Jan-17				■ Removal of 4th layer and 5th layer ELS								
A2270	Removal of 4th layer and 5th layer ELS	6d	07-Jan-17	13-Jan-17				■ Removal of 4th layer and 5th layer ELS								
A2250	Removal of 4th layer and 5th layer ELS	6d	08-Jan-17	14-Jan-17				■ Removal of 4th layer and 5th layer ELS								
A2240	Bay SR4 Walls	7d	13-Jan-17	19-Jan-17				■ Bay SR4 Walls								
A2280	Bay SR6 Walls	7d	13-Jan-17	20-Jan-17				■ Bay SR6 Walls								
A2260	Bay SR5 Walls	7d	14-Jan-17	21-Jan-17				■ Bay SR5 Walls								
A2290	Removal of 5th layer ELS	4d	16-Jan-17	19-Jan-17				■ Removal of 5th layer ELS								
A2300	Bay SR7 Walls	5d	20-Jan-17	24-Jan-17				■ Bay SR7 Walls								
A2210	Removal of 4th layer and 5th layer ELS	4d	25-Jan-17	28-Jan-17				■ Removal of 4th layer and 5th layer ELS								
A2220	Bay SR3 Walls	5d	29-Jan-17	02-Feb-17				■ Bay SR3 Walls								
OHVD Structure, Maintenance Walkway and Profile Barrier of SR8 - 2000 m3		35d	04-Jan-17	07-Feb-17												
A2320	Bay SR1R OHVD, Maintenance Walkway and Profile Barrier	7d	04-Jan-17*	10-Jan-17				■ Bay SR1R OHVD, Maintenance Walkway and Profile Barrier								
A2380	Removal of 5th Layer ELS	5d	07-Jan-17	11-Jan-17				■ Removal of 5th Layer ELS								
A2390	Bay SR8R OHVD, Maintenance Walkway and Profile Barrier	4d	12-Jan-17	15-Jan-17				■ Bay SR8R OHVD, Maintenance Walkway and Profile Barrier								
A2340	Bay SR4R OHVD, Maintenance Walkway and Profile Barrier	5d	20-Jan-17	24-Jan-17				■ Bay SR4R OHVD, Maintenance Walkway and Profile Barrier								
A2360	Bay SR6R OHVD, Maintenance Walkway and Profile Barrier	4d	20-Jan-17	24-Jan-17				■ Bay SR6R OHVD, Maintenance Walkway and Profile Barrier								
A2350	Bay SR5R OHVD, Maintenance Walkway and Profile Barrier	7d	21-Jan-17	28-Jan-17				■ Bay SR5R OHVD, Maintenance Walkway and Profile Barrier								
A2370	Bay SR7R OHVD, Maintenance Walkway and Profile Barrier	4d	25-Jan-17	28-Jan-17				■ Bay SR7R OHVD, Maintenance Walkway and Profile Barrier								
A2330	Bay SR3R OHVD, Maintenance Walkway and Profile Barrier	5d	03-Feb-17	07-Feb-17				■ Bay SR3R OHVD, Maintenance Walkway and Profile Barrier								
Top Slab of SR8 - 12000 m3		37d	11-Jan-17	16-Feb-17												
A2400	Bay SR1R	10d	11-Jan-17	20-Jan-17				■ Bay SR1R								
A2460	Bay SR8R	9d	16-Jan-17	24-Jan-17				■ Bay SR8R								
A2440	Bay SR6R	9d	24-Jan-17	02-Feb-17				■ Bay SR6R								
A2420	Bay SR4R	6d	25-Jan-17	30-Jan-17				■ Bay SR4R								
A2430	Bay SR5R	8d	28-Jan-17	05-Feb-17				■ Bay SR5R								
A2450	Bay SR7R	9d	29-Jan-17	06-Feb-17				■ Bay SR7R								
A2410	Bay SR3R	7d	10-Feb-17	16-Feb-17				■ Bay SR3R								
Earthwork Backfilling, ELS Removal and Water Recharging		122d	10-Nov-16 A	11-Mar-17												
East Portion		116d	10-Nov-16 A	05-Mar-17												

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan		Feb		Mar			Apr	
A2470	Stage 1 Backfilling- 6000 m3 (-30 mPD~ -20 mPD, Bay 2 -Bay 4) - 500 m3 per day	13d	10-Nov-16 A	17-Jan-17				Stage:1 Backfilling- 6000 m3 (-30mPD~ -20 mPD, Bay 2 -Bay 4) - 500 m3 per day								
A2480	Stage 2 Backfilling- 28000 m3 (-20 mPD~ -10 mPD, Bay 2- Bay 4) - 1560 m3 per day	18d	18-Jan-17	04-Feb-17					Stage 2 Backfilling- 28000 m3 (-20 mPD~ -10 mPD, Bay 2- Bay 4) - 1560 m3 per day							
A2490	Stage 3 Backfilling- 18000 m3 (-10mPD~ -7.0 mPD, Bay 2- Bay 4) - 1000 m3 per day	18d	05-Feb-17	22-Feb-17						Stage 3 Backfilling- 18000 m3 (-10mPD~ -7.0 mPD, Bay 2- Bay 4) - 1000 m3 per day						
A2510	Closure of wall opening in Bay 1 of CCT (Wall 4 and Wall 5)	11d	12-Feb-17	23-Feb-17							Closure of wall opening in Bay 1 of CCT (Wall 4 and Wall 5)					
A2520	Stage 5 Backfilling ~ 10000 m3 (-30 mPD ~ -7.0 mPD, Bay 1) ~ 1000 m3 per day	11d	18-Feb-17	28-Feb-17							Stage 5 Backfilling ~ 10000 m3 (-30 mPD ~ -7.0 mPD, Bay 1) ~ 1000 m3 per day					
A2500	Removal of 2nd Layer ELS and Removal of Reprop inside Tunnel (Bay 2- Bay 4)	10d	23-Feb-17	04-Mar-17								Removal of 2nd Layer ELS and Removal of Reprop inside Tunnel (Bay 2- Bay 4)				
A2515	Backfilling of Bay 1	11d	23-Feb-17	05-Mar-17								Backfilling of Bay 1				
A2530	Removal of 2nd Layer ELS (Bay 1)	5d	01-Mar-17	05-Mar-17								Removal of 2nd Layer ELS (Bay 1)				
West Portion		33d	13-Jan-17	14-Feb-17												
A2540	Stage 4 Backfilling - 69000 m3 (-30mPD~ -7.0 mPD, Bay 5-8) - 2500 m3 per day	28d	13-Jan-17	09-Feb-17				Stage 4 Backfilling - 69000 m3 (-30mPD~ -7.0 mPD, Bay 5-8) - 2500 m3 per day								
A2550	Removal of 2nd Layer ELS - 10 days	13d	02-Feb-17	14-Feb-17					Removal of 2nd Layer ELS - 10 days							
Water Recharge (CNY- 27/1~ 2/2)		6d	06-Mar-17	11-Mar-17												
A2560	Water Re-charge to ELS Cofferdam	6d	06-Mar-17	11-Mar-17								Water Re-charge to ELS Cofferdam				
Skin Wall Removal Works between TS4/TS3W and Shaft D Closure		85d	30-Dec-16	24-Mar-17												
A2570	Design Review and ICE Cert for 1st Stage Skin Wall Removal	15d	30-Dec-16	13-Jan-17			Design Review and ICE Cert for 1st Stage Skin Wall Removal									
A2580	Skin Wall Removal Works between TS4/TS3W - 20 days (1st stage) - SR8	20d	14-Jan-17	02-Feb-17				Skin Wall Removal Works between TS4/TS3W - 20 days (1st stage) - SR8								
A2590	Skin Wall Removal Works between TS4/TS3W - 20 days (2nd stage) - After Tunnel Roof Slab Completion - E/B and W/B	20d	03-Feb-17	22-Feb-17					Skin Wall Removal Works between TS4/TS3W - 20 days (2nd stage) - After Tunnel Roof Slab Completion - E/B and W/B							
A2600	Construction of Remaining Tunnel Structure between CH. 4260.2- 4265.2 at SOL T100 for Mainline E/B, W/B, SR8	30d	23-Feb-17	24-Mar-17							Construction of Remaining Tunnel Structure between CH. 4260.2- 4265.2 at SOL T100 for Mainline E/B, W/B, SR8					
A2610	Shaft D R/C Slab Reinstatement	20d	23-Feb-17	14-Mar-17							Shaft D R/C Slab Reinstatement					
Removal Bulkhead at CH525 (TS3W / SR8 Junction)		51d	21-Jan-17	12-Mar-17												
A4830	Curing Period for Removal of Scaffolding of Bay SR1R of SR8 Roof Slab	10d	21-Jan-17	30-Jan-17					Curing Period for Removal of Scaffolding of Bay SR1R of SR8 Roof Slab							
A5180	Remove Scaffolding of SR1R Roof	4d	31-Jan-17	03-Feb-17					Remove Scaffolding of SR1R Roof							
A6080	Remove Bulkhead between TS3W & SR8	37d	04-Feb-17	12-Mar-17						Remove Bulkhead between TS3W & SR8						
Works in KD8		66d	27-Jan-17	02-Apr-17												
TS3W - Remove Temporary Reclamation		66d	27-Jan-17	02-Apr-17												
Stage 1 - North West Corner (Bay Z4-25 to Bay 20)		24d	27-Jan-17	19-Feb-17												
A2650	Break concrete slab at Bay Z4-25 to Bay 20	4d	27-Jan-17	30-Jan-17					Break concrete slab at Bay Z4-25 to Bay 20							
A2660	Remove filled material to -4.35mPD at Bay Z4-25 to Bay 19 (6,500m3)	8d	31-Jan-17	07-Feb-17					Remove filled material to -4.35mPD at Bay Z4-25 to Bay 19 (6,500m3)							
A2670	Remove seawall blocks at Bay Z4-25 to Bay 20 (426 nos.)	8d	08-Feb-17	15-Feb-17					Remove seawall blocks at Bay Z4-25 to Bay 20 (426 nos.)							
A2680	Remove filled material to -7.0 mPD	4d	16-Feb-17	19-Feb-17					Remove filled material to -7.0 mPD							
Stage 2 - North to East Side (Bay 19 to Bay 11 + Bay 26 to Bay 28)		14d	31-Jan-17	13-Feb-17												
A2690	Break concrete slab at Bay 19 to Bay 11 + Bay 26 to Bay 28 (2,500m2)	7d	31-Jan-17	06-Feb-17					Break concrete slab at Bay 19 to Bay 11 + Bay 26 to Bay 28 (2,500m2)							
A2700	Remove filled material to +2.8mPD (2,500m3)	7d	07-Feb-17	13-Feb-17					Remove filled material to +2.8mPD (2,500m3)							
Stage 3 - North to East Side (Bay 19 to bay 26)		22d	12-Mar-17	02-Apr-17												
North West D-wall Opening		19d	12-Mar-17	30-Mar-17												
A2720	Core D-wall cut holes at Panel DW02 to NA6 (27 nos.)	4d	12-Mar-17	15-Mar-17							Core D-wall cut holes at Panel DW02 to NA6 (27 nos.)					
A2730	Vertical cut at Panel DW02 to NA6 (19 nos.)	8d	16-Mar-17	23-Mar-17							Vertical cut at Panel DW02 to NA6 (19 nos.)					
A2740	Horizontal cut at Panel DW02 to NA6 (25 nos.)	7d	24-Mar-17	30-Mar-17							Horizontal cut at Panel DW02 to NA6 (25 nos.)					
North East & East		22d	12-Mar-17	02-Apr-17												
A2750	Remove filled material to -4.35mPD (22,500m3)	9d	12-Mar-17	20-Mar-17							Remove filled material to -4.35mPD (22,500m3)					
A2760	Remove seawall blocks at Bay 19 to 11 & Bay 26 to 28 (1,335 nos.)	13d	21-Mar-17	02-Apr-17							Remove seawall blocks at Bay 19 to 11 & Bay 26 to 28 (1,335 nos.)					
Works in KD6		333d	19-Apr-16 A	18-Mar-17												
Works in SR8 (Open Cut Method)		333d	19-Apr-16 A	18-Mar-17												
SR8 (Zone C) - Ch. 528 to Ch. 368		109d	18-Nov-16 A	18-Mar-17												

Activity ID	Activity Name	Original Duration	Start	Finish	2016		2017															
					Dec		Jan				Feb					Mar				Apr		
ELS		46d	19-Nov-16 A	04-Jan-17																		
Area B (CH475 to CH514) - steel Deck EB + SR8/TS3 Interface		46d	19-Nov-16 A	04-Jan-17																		
Strut & Waling Installation for SL5		41d	19-Nov-16 A	07-Dec-16 A																		
A3470	Area B - Waling Installation	6d	19-Nov-16 A	02-Dec-16 A	tion																	
A3480	Area B - Srrtut Installation for SL5	9d	30-Nov-16 A	03-Dec-16 A	ation for SL5																	
A1621	Area B - Bracing Installation for Layer 2 (Bottom Horizontal & Diagonal)	1d	07-Dec-16 A	07-Dec-16 A	ing Installation for Layer 2 (Bottom Horizontal & Diagonal)																	
Excavation to -17.9mPD From SL5 to Formation (3,908 m3 / 540m3/D approx.3.3m Depth)		34d	30-Nov-16 A	05-Dec-16 A																		
A3440	Area B - Excavation 1st cycle (1.2m Depth) & Lagging Plate	4d	30-Nov-16 A	01-Dec-16 A	ycle (1.2m Depth) & Lagging Plate																	
A3450	Area B - Excavation 2nd cycle (1.2m Depth) & Lagging Plate	4d	02-Dec-16 A	03-Dec-16 A	nd cycle (1.2m Depth) & Lagging Plate																	
A3460	Area B - Excavation 3rd cycle (0.9m Depth) & Lagging Plate	3d	04-Dec-16 A	05-Dec-16 A	on 3rd cycle (0.9m Depth) & Lagging Plate																	
Excavation for Rock Fill (1000mm Below F.L./1,576 m3/ 540m3/D)		6d	30-Dec-16	04-Jan-17																		
A3490	Area B - Excavation further down to 1000mm below F.L.	1d	30-Dec-16	30-Dec-16	Area B - Excavation further down to 1000mm below F.L.																	
A3500	Area B - Lay & Compact Rock Fill	4d	31-Dec-16	03-Jan-17	Area B - Lay & Compact Rock Fill																	
A3510	Area B - Blinding / Divert Ground Water by Submerge Pump	2d	03-Jan-17	04-Jan-17	Area B - Blinding /Divert Ground Water by Submerge Pump																	
Tunnel Structure		108d	18-Nov-16 A	18-Mar-17																		
Area A (CH384 to CH475 - Victoria Park to Steel Deck WB + IEC)		97d	18-Nov-16 A	07-Mar-17																		
Vertical Blinding Bay C1 to C4		13d	29-Nov-16 A	09-Dec-16 A																		
A4300	Bay C4	13d	29-Nov-16 A	09-Dec-16 A																		
Tunnel Structure at Area A - Bay C1 to C4		97d	18-Nov-16 A	07-Mar-17																		
Bay C2		89d	30-Nov-16 A	05-Mar-17																		
Structure		41d	30-Nov-16 A	16-Jan-17																		
1.2m Thick Base Slab		26d	30-Nov-16 A	16-Dec-16 A																		
T1350	C2 Base - Concreting	1d	30-Nov-16 A	30-Nov-16 A																		
T1370	C2 Base - Remove 3th & 5th Strut SL3 & SL5 (2 Nos@SL5 & 8 Nos@SL3)	3d	09-Dec-16 A	16-Dec-16 A	C2 Base - Remove 3th & 5th Strut SL3 & SL5 (2 Nos@SL5 & 8 Nos@SL3)																	
1m Thick Tunnel Wall at Both Sides & OHVD Slab		7d	22-Dec-16 A	04-Jan-17																		
T1380	C2 Wall & OHVD - Erect Scaffolding & Soffit Formwork	4d	22-Dec-16 A	30-Dec-16	C2 Wall & OHVD - Erect Scaffolding & Soffit Formwork																	
T1390	C2 Wall & OHVD - Steel Fixing & Wall Formwork	5d	30-Dec-16	03-Jan-17	C2 Wall & OHVD - Steel Fixing & Wall Formwork																	
T1400	C2 Wall & OHVD - Concreting	1d	04-Jan-17	04-Jan-17	C2 Wall & OHVD - Concreting																	
400mm Thick OHVD Hanger Wall & 1.2m Thick Top Slab		12d	05-Jan-17	16-Jan-17																		
T1440	C2 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork	3d	05-Jan-17	07-Jan-17	C2 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork																	
T1450	C2 OHVD Hanger Wall & Roof - Steel Fixing (+1 d for Wall Steel fixing)	6d	08-Jan-17	13-Jan-17	C2 OHVD Hanger Wall & Roof - Steel Fixing (+1 d for Wall Steel fixing)																	
T1460	C2 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop	2d	14-Jan-17	15-Jan-17	C2 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop																	
T1470	C2 OHVD Hanger Wall & Roof - Concreting	1d	16-Jan-17	16-Jan-17	C2 OHVD Hanger Wall & Roof - Concreting																	
Removal of Falseworks & SL4		23d	17-Jan-17	08-Feb-17																		
T1550	C2 Roof - 10 Days Curing of Roof Prior to Removal of Falsework	10d	17-Jan-17	26-Jan-17	C2 Roof - 10 Days Curing of Roof Prior to Removal of Falsework																	
T1560	C2 Roof - Remove Falsework	6d	27-Jan-17	05-Feb-17	C2 Roof - Remove Falsework																	
T2730	C2 Wall - Remove Strut SL4 (8 No / Layer/ Bay C2)	3d	06-Feb-17	08-Feb-17	C2 Wall - Remove Strut SL4 (8 No / Layer/ Bay C2)																	
Egress Passage		17d	08-Feb-17	25-Feb-17																		
Wall of EP		9d	08-Feb-17	17-Feb-17																		
A3780	C2 Erect Scaffolding & working Platform	1d	08-Feb-17	09-Feb-17	C2 Erect Scaffolding & working Platform																	
A3750	C2 Internal Wall Formwork	2d	09-Feb-17	11-Feb-17	C2 Internal Wall Formwork																	
A3760	C2 Steel Fixing to Wall	2d	11-Feb-17	13-Feb-17	C2 Steel Fixing to Wall																	
A3770	C2 External Wall Formwork	3d	13-Feb-17	16-Feb-17	C2 External Wall Formwork																	
A3790	C2 Concrete to Wall	1d	16-Feb-17	17-Feb-17	C2 Concrete to Wall																	

Activity ID		Activity Name	Original Duration	Start	Finish	2016												2017																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
						Dec						Jan						Feb						Mar						Apr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
Bay C1	Roof of EP		8d	17-Feb-17	25-Feb-17																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	</

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan			Feb			Mar		Apr
A3690	C1 Side Fromwork for Wall up to Roof Top	2d	23-Feb-17	24-Feb-17										C1 Side Fromwork for Wall up to Roof Top		
A3700	C1 Concrete to Roof	1d	25-Feb-17	25-Feb-17										C1 Concrete to Roof		
Utility Trough		25d	09-Feb-17	05-Mar-17												
Left Hand Side		8d	26-Feb-17	05-Mar-17												
A3720	C1 - LHS Backing Concrete of Utility Trough	4d	26-Feb-17	01-Mar-17										C1 - LHS Backing Concrete of Utility Trough		
A3710	C1 - LHS Profile Barrier of Utility Trough	4d	02-Mar-17	05-Mar-17										C1 - LHS Profile Barrier of Utility Trough		
Right Hand Side		8d	09-Feb-17	16-Feb-17												
A3730	C1 - RHS Backing Concrete of Utility Trough	4d	09-Feb-17	12-Feb-17							C1 - RHS Backing Concrete of Utility Trough					
A3740	C1 - RHS Profile Barrier of Utility Trough	4d	13-Feb-17	16-Feb-17							C1 - RHS Profile Barrier of Utility Trough					
Bay C3		67d	02-Dec-16 A	06-Mar-17												
Structure		20d	02-Dec-16 A	18-Jan-17												
A4290	Fixing T-Grid Waterproofing on Base Slab & Vertical Blinding	3d	02-Dec-16 A	07-Dec-16 A	Waterproofing on Base Slab & Vertical Blinding											
1.2m Thick Base Slab		12d	08-Dec-16 A	24-Dec-16 A												
T2950	C3 Base - Rebar Fixing	5d	08-Dec-16 A	13-Dec-16 A	C3 Base - Rebar Fixing											
T2960	C3 Base - Kicker Formwork & Water Stop	2d	14-Dec-16 A	14-Dec-16 A	C3 Base - Kicker Formwork & Water Stop											
T2970	C3 Base - Concreting	1d	15-Dec-16 A	15-Dec-16 A	C3 Base - Concreting											
T2980	C3 Base - Remove Kicker Formwork & Make Good C.J.	1d	16-Dec-16 A	16-Dec-16 A	C3 Base - Remove Kicker Formwork & Make Good C.J.											
T2990	C3 Base - Remove 3th & 5th Strut SL3 & SL5 (1 Nos@SL5 & 8 Nos@SL3)	3d	17-Dec-16 A	24-Dec-16 A	C3 Base - Remove 3th & 5th Strut SL3 & SL5 (1 Nos@SL5 & 8 Nos@SL3)											
1m Thick Tunnel Wall at Both Sides & OHVD Slab		9d	30-Dec-16	07-Jan-17												
T3000	C3 Wall & OHVD - Erect Scaffolding & Soffit Formwork	3d	30-Dec-16	01-Jan-17			C3 Wall & OHVD - Erect Scaffolding & Soffit Formwork									
T3010	C3 Wall & OHVD - Steel Fixing	4d	02-Jan-17	05-Jan-17			C3 Wall & OHVD - Steel Fixing									
T3020	C3 Wall & OHVD - Wall Formwork + Side Formwork for OHVD Slab	1d	06-Jan-17	06-Jan-17			C3 Wall & OHVD - Wall Formwork + Side Formwork for OHVD Slab									
T3030	C3 Wall & OHVD - Concreting	1d	07-Jan-17	07-Jan-17			C3 Wall & OHVD - Concreting									
400mm Thick OHVD Hanger Wall & 1.2m Thick Top Slab		11d	08-Jan-17	18-Jan-17												
T3040	C3 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork	3d	08-Jan-17	10-Jan-17			C3 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork									
T3050	C3 OHVD Hanger Wall & Roof - Steel Fixing (+1 D for Wall Steel Fixing)	6d	11-Jan-17	16-Jan-17			C3 OHVD Hanger Wall & Roof - Steel Fixing (+1 D for Wall Steel Fixing)									
T3060	C3 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop	1d	17-Jan-17	17-Jan-17			C3 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop									
T3080	C3 OHVD Hanger Wall & Roof - Concreting	1d	18-Jan-17	18-Jan-17			C3 OHVD Hanger Wall & Roof - Concreting									
Removal of Falseworks & SL4		22d	19-Jan-17	09-Feb-17												
T1790	C3 Roof - 10 Days Curing of Roof Prior to Removal of Falsework	10d	19-Jan-17	28-Jan-17				C3 Roof - 10 Days Curing of Roof Prior to Removal of Falsework								
T1800	C3 Roof - Remove Falsework	6d	01-Feb-17	06-Feb-17				C3 Roof - Remove Falsework								
T2750	C3 Wall - Remove Strut SL4 (8 No / Layer/ Bay C3)	3d	07-Feb-17	09-Feb-17				C3 Wall - Remove Strut SL4 (8 No / Layer/ Bay C3)								
Egress Passage		17d	10-Feb-17	26-Feb-17												
Wall of EP		9d	10-Feb-17	18-Feb-17												
A2310	C3 Erect Scaffolding & working Platform	1d	10-Feb-17	10-Feb-17							C3 Erect Scaffolding & working Platform					
A3920	C3 Internal Wall Formwork	2d	11-Feb-17	12-Feb-17							C3 Internal Wall Formwork					
A3930	C3 Steel Fixing to Wall	2d	13-Feb-17	14-Feb-17							C3 Steel Fixing to Wall					
A3940	C3 External Wall Formwork	3d	15-Feb-17	17-Feb-17							C3 External Wall Formwork					
A3950	C3 Concrete to Wall	1d	18-Feb-17	18-Feb-17							C3 Concrete to Wall					
Roof of EP		8d	19-Feb-17	26-Feb-17												
A3960	C3 Scaffolding & Soffit Formwork	3d	19-Feb-17	21-Feb-17							C3 Scaffolding & Soffit Formwork					
A3970	C3 Steel Fixing to Roof	2d	22-Feb-17	23-Feb-17							C3 Steel Fixing to Roof					
A3980	C3 Side Fromwork for Wall up to Roof Top	2d	24-Feb-17	25-Feb-17							C3 Side Fromwork for Wall up to Roof Top					
A3990	C3 Concrete to Roof	1d	26-Feb-17	26-Feb-17							C3 Concrete to Roof					

Activity ID	Activity Name	Original Duration	Start	Finish																	
					2016				2017												
					Dec				Jan					Feb				Mar			Apr
	Utility Trough	25d	10-Feb-17	06-Mar-17																	
	Left Hand Side	8d	27-Feb-17	06-Mar-17																	
A4000	C3 - LHS Backing Concrete of Utility Trough	4d	27-Feb-17	02-Mar-17																	
A4010	C3 - LHS Profile Barrier of Utility Trough	4d	03-Mar-17	06-Mar-17																	
	Right Hand Side	8d	10-Feb-17	17-Feb-17																	
A4020	C3 - RHS Backing Concrete of Utility Trough	4d	10-Feb-17	13-Feb-17																	
A4030	C3 - RHS Profile Barrier of Utility Trough	4d	14-Feb-17	17-Feb-17																	
	Bay C4	67d	14-Dec-16 A	07-Mar-17																	
	Structure	24d	14-Dec-16 A	22-Jan-17																	
A4310	Fixing T-Grid Waterproofing on Base Slab & Vertical Blinding	3d	14-Dec-16 A	18-Dec-16 A																	
	1.2m Thick Base Slab	9d	19-Dec-16 A	02-Jan-17																	
T3120	C4 Base - Rebar Fixing	3d	19-Dec-16 A	21-Dec-16 A																	
T3130	C4 Base - Kicker Formwork & Water Stop	2d	22-Dec-16 A	22-Dec-16 A																	
T3140	C4 Base - Concreting	1d	23-Dec-16 A	23-Dec-16 A																	
T3160	C4 Base - Remove 3th & 5th Strut SL3 & SL5 (3 Nos@SL5 & 8 Nos@SL3)	4d	30-Dec-16	02-Jan-17																	
	1m Thick Tunnel Wall at Both Sides & OHVD Slab	11d	02-Jan-17	13-Jan-17																	
T3170	C4 Wall & OHVD - Erect Scaffolding & Soffit Formwork	4d	02-Jan-17	06-Jan-17																	
T3180	C4 Wall & OHVD - Steel Fixing	5d	06-Jan-17	11-Jan-17																	
T3190	C4 Wall & OHVD - Wall Formwork + Side Formwork for OHVD Slab	1d	11-Jan-17	12-Jan-17																	
T3200	C4 Wall & OHVD - Concreting	1d	12-Jan-17	13-Jan-17																	
	400mm Thick OHVD Hanger Wall & 1.2m Thick Top Slab	9d	13-Jan-17	22-Jan-17																	
T3210	C4 OHVD Hanger Wall & Roof - Erect Faslework & Soffit Formworks + Hanger Wall Formwork	3d	13-Jan-17	16-Jan-17																	
T3220	C4 OHVD Hanger Wall & Roof - Steel Fixing (+1 D for Wall Fixing)	4d	16-Jan-17	20-Jan-17																	
T3230	C4 OHVD Hanger Wall & Roof - Top slab CJ Formwork Erection & Water Stop	1d	20-Jan-17	21-Jan-17																	
T3250	C4 OHVD Hanger Wall & Roof - Concreting	1d	21-Jan-17	22-Jan-17																	
	Removal of Falseworks & SL5	19d	22-Jan-17	10-Feb-17																	
T3300	C4 Roof - 10 Days Curing of Roof Prior to Removal of Falsework	10d	22-Jan-17	01-Feb-17																	
T3310	C4 Roof - Remove Falsework	6d	01-Feb-17	07-Feb-17																	
T3290	C4 Wall - Remove Strut SL4 (8 No / Layer/ Bay C3)	3d	07-Feb-17	10-Feb-17																	
	Egress Passage	17d	10-Feb-17	27-Feb-17																	
	Wall of EP	9d	10-Feb-17	19-Feb-17																	
A4140	C4 Erect Scaffolding & working Platform	1d	10-Feb-17	11-Feb-17																	
A4110	C4 Internal Wall Formwork	2d	11-Feb-17	13-Feb-17																	
A4120	C4 Steel Fixing to Wall	2d	13-Feb-17	15-Feb-17																	
A4130	C4 External Wall Formwork	3d	15-Feb-17	18-Feb-17																	
A4150	C4 Concrete to Wall	1d	18-Feb-17	19-Feb-17																	
	Roof of EP	8d	19-Feb-17	27-Feb-17																	
A4160	C4 Scaffolding & Soffit Formwork	3d	19-Feb-17	22-Feb-17																	
A4170	C4 Steel Fixing to Roof	2d	22-Feb-17	24-Feb-17																	
A4180	C4 Side Fromwork for Wall up to Roof Top	2d	24-Feb-17	26-Feb-17																	
A4190	C4 Concrete to Roof	1d	26-Feb-17	27-Feb-17																	
	Utility Trough	25d	10-Feb-17	07-Mar-17																	
	Left Hand Side	8d	27-Feb-17	07-Mar-17																	
A4200	C4 - LHS Backing Concrete of Utility Trough	4d	27-Feb-17	03-Mar-17																	

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan			Feb			Mar		
	A4210	C4 - LHS Profile Barrier of Utility Trough	4d	03-Mar-17	07-Mar-17											C4 - LHS Profile Barrier of Utility Trough
	Right Hand Side		8d	10-Feb-17	18-Feb-17											
	A4220	C4 - RHS Backing Concrete of Utility Trough	4d	10-Feb-17	14-Feb-17											C4 - RHS Backing Concrete of Utility Trough
	A4230	C4 - RHS Profile Barrier of Utility Trough	4d	14-Feb-17	18-Feb-17											C4 - RHS Profile Barrier of Utility Trough
	Area B (CH475 to CH514) - steel Deck EB + SR8/TS3 Interface		76d	15-Dec-16 A	18-Mar-17											
	Vertical Blinding Bay C5 to Bay C6		13d	15-Dec-16 A	31-Dec-16											
	A4320	Bay C5	13d	15-Dec-16 A	31-Dec-16											
	Tunnel Structure at Area B - Bay C5 to C6		76d	01-Jan-17	18-Mar-17											
	Bay C5		68d	01-Jan-17	10-Mar-17											
	Structure		36d	01-Jan-17	06-Feb-17											
	1.2m Thick Base Slab		7d	01-Jan-17	07-Jan-17											
	T3350	C5 Base - Rebar Fixing	3d	01-Jan-17	03-Jan-17											C5 Base - Rebar Fixing
	T3360	C5 Base - Kicker Formwork & Water Stop	1d	04-Jan-17	04-Jan-17											C5 Base - Kicker Formwork & Water Stop
	T3370	C5 Base - Concreting	1d	05-Jan-17	05-Jan-17											C5 Base - Concreting
	T3390	C5 Base - Remove 6th Strut SL5 (5 Nos@SL5)	2d	06-Jan-17	07-Jan-17											C5 Base - Remove 6th Strut SL5 (5 Nos@SL5)
	1m Thick Tunnel Wall at Both Sides		15d	07-Jan-17	22-Jan-17											
	T3400	C5 Wall & OHVD - Erect Working Platform	1d	07-Jan-17	08-Jan-17											C5 Wall & OHVD - Erect Working Platform
	T3410	C5 Wall & OHVD - Steel Fixing	5d	08-Jan-17	13-Jan-17											C5 Wall & OHVD - Steel Fixing
	T3420	C5 Wall - Internal Formwork & Water Stop	3d	13-Jan-17	16-Jan-17											C5 Wall - Internal Formwork & Water Stop
	T3430	C5 Wall & OHVD - Concreting of Wall	1d	16-Jan-17	17-Jan-17											C5 Wall & OHVD - Concreting of Wall
	T3480	C5 Wall - Remove Wall Formwork	2d	17-Jan-17	19-Jan-17											C5 Wall - Remove Wall Formwork
	T3540	C5 Wall - Remove 3th & 4th Strut SL3 & SL4 (5 Nos@SL3 & 5 Nos@SL4)	3d	19-Jan-17	22-Jan-17											C5 Wall - Remove 3th & 4th Strut SL3 & SL4 (5 Nos@SL3 & 5 Nos@SL4)
	OHVD Slab		6d	22-Jan-17	28-Jan-17											
	T3440	C5 OHVD - Erect Falsework	1d	22-Jan-17	23-Jan-17											C5 OHVD - Erect Falsework
	T3450	C5 OHVD - Erect Soffit Formwork	2d	23-Jan-17	25-Jan-17											C5 OHVD - Erect Soffit Formwork
	T3460	C5 OHVD - Steel Fixing for Slab	2d	25-Jan-17	27-Jan-17											C5 OHVD - Steel Fixing for Slab
	T3470	C5 OHVD - Placing Concrete to OHVD Slab	1d	27-Jan-17	28-Jan-17											C5 OHVD - Placing Concrete to OHVD Slab
	400mm Thick OHVD Hanger Wall & 1.2m Thick Top Slab		9d	28-Jan-17	06-Feb-17											
	T3490	C5 OHVD - Steel Fixing for Hanger Wall	1d	28-Jan-17	29-Jan-17											C5 OHVD - Steel Fixing for Hanger Wall
	T3500	C5 OHVD - Erect Formwork for Hanger Wall	1d	29-Jan-17	30-Jan-17											C5 OHVD - Erect Formwork for Hanger Wall
	T3510	C5 Roof - Erect Falsework & Soffit Formwork	3d	30-Jan-17	02-Feb-17											C5 Roof - Erect Falsework & Soffit Formwork
	T3520	C5 Roof - Steel Fixing (Wall Steel Fixing Completed together with Roof)	3d	02-Feb-17	05-Feb-17											C5 Roof - Steel Fixing (Wall Steel Fixing Completed together with Roof)
	T3530	C5 Roof - Placing Concrete to Roof Slab & OHVD Hanger Wall	1d	05-Feb-17	06-Feb-17											C5 Roof - Placing Concrete to Roof Slab & OHVD Hanger Wall
	Removal of Falseworks & SL5		16d	06-Feb-17	22-Feb-17											
	T3330	C5 Roof - 10 Days Curing of Roof Prior to Removal of Falsework	10d	06-Feb-17	16-Feb-17											C5 Roof - 10 Days Curing of Roof Prior to Removal of Falsework
	T3340	C5 Roof - Remove Falsework	6d	16-Feb-17	22-Feb-17											C5 Roof - Remove Falsework
	Utility Trough		16d	22-Feb-17	10-Mar-17											
	Left Hand Side		8d	02-Mar-17	10-Mar-17											
	A4080	C5 - LHS Backing Concrete of Utility Trough	4d	02-Mar-17	06-Mar-17											C5 - LHS Backing Concrete of Utility Trough
	A4070	C5 - LHS Profile Barrier of Utility Trough	4d	06-Mar-17	10-Mar-17											C5 - LHS Profile Barrier of Utility Trough
	Right Hand Side		8d	22-Feb-17	02-Mar-17											
	A4090	C5 - RHS Backing Concrete of Utility Trough	4d	22-Feb-17	26-Feb-17											C5 - RHS Backing Concrete of Utility Trough
	A4100	C5 - RHS Profile Barrier of Utility Trough	4d	26-Feb-17	02-Mar-17											C5 - RHS Profile Barrier of Utility Trough
	Bay C6		70d	07-Jan-17	18-Mar-17											

Activity ID	Activity Name	Original Duration	Start	Finish	2016		2017																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
					Dec		Jan				Feb				Mar				Apr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
SR8 (Zone B) - Ch.385.000 to Ch.317.500 - (Inside Victoria Park to Tunnel Portal)	Structure	39d	07-Jan-17	15-Feb-17																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016			2017								
					Dec			Jan		Feb			Mar			Apr
	SR8_ZB_1480	Zone B - OHVD Bay 3 - Rebar Fixing for Slab of OHVD	3d	24-Jan-17	26-Jan-17					Zone B - OHVD Bay 3 - Rebar Fixing for Slab of OHVD						
	SR8_ZB_1490	Zone B - OHVD Bay 3 - Concrete of Slab of OHVD	1d	27-Jan-17	27-Jan-17					Zone B - OHVD Bay 3 - Concrete of Slab of OHVD						
	SR8_ZB_1530	Zone B - OHVD Bay 3 - Curing Period for OHVD Slab	10d	28-Jan-17	06-Feb-17					Zone B - OHVD Bay 3 - Curing Period for OHVD Slab						
	SR8_ZB_1500	Zone B - OHVD Bay 3 - Rebar Fixing to Hanger Wall	1d	01-Feb-17	01-Feb-17					Zone B - OHVD Bay 3 - Rebar Fixing to Hanger Wall						
	SR8_ZB_1510	Zone B - OHVD Bay 3 - Erect Hanger Wall Formwork for OHVD	2d	02-Feb-17	03-Feb-17					Zone B - OHVD Bay 3 - Erect Hanger Wall Formwork for OHVD						
	SR8_ZB_1520	Zone B - OHVD Bay 3 - Concrete Hanger Wall of OHVDV	1d	04-Feb-17	04-Feb-17					Zone B - OHVD Bay 3 - Concrete Hanger Wall of OHVDV						
	SR8_ZB_1540	Zone B - OHVD Bay 3 - Remove Soffit Formwork & Scaffolding	5d	07-Feb-17	11-Feb-17					Zone B - OHVD Bay 3 - Remove Soffit Formwork & Scaffolding						
	Utility Trough		28d	30-Dec-16	04-Feb-17											
	Left Hand Side		21d	09-Jan-17	04-Feb-17											
	SR8_ZB_1570	Zone B - U trough (LHS) Bay 3	7d	09-Jan-17	16-Jan-17			Zone B : U trough (LHS) Bay 3								
	SR8_ZB_1560	Zone B - U trough (LHS) Bay 2	7d	17-Jan-17	24-Jan-17			Zone B - U trough (LHS) Bay 2								
	SR8_ZB_1550	Zone B - U trough (LHS) Bay 1	7d	25-Jan-17	04-Feb-17					Zone B - U trough (LHS) Bay 1						
	Right Hand Side		21d	30-Dec-16	24-Jan-17											
	SR8_ZB_1600	Zone B - U trough (RHS) Bay 3	7d	30-Dec-16*	07-Jan-17		Zone B - U trough (RHS) Bay 3									
	SR8_ZB_1590	Zone B - U trough (RHS) Bay 2	7d	09-Jan-17	16-Jan-17		Zone B : U trough (RHS) Bay 2									
	SR8_ZB_1580	Zone B - U trough (RHS) Bay 1	7d	17-Jan-17	24-Jan-17			Zone B - U trough (RHS) Bay 1								
	Pump House		53d	30-Dec-16	20-Feb-17											
	Pressure Relief Manhole		14d	26-Jan-17	15-Feb-17											
	SR8_ZB_1800	PS- Manhole Internal Wall Formwork	4d	26-Jan-17	03-Feb-17					PS- Manhole Internal Wall Formwork						
	SR8_ZB_1810	PS- Erect Scaffolding + Roof Soffit Formwork	5d	03-Feb-17	09-Feb-17					PS- Erect Scaffolding + Roof Soffit Formwork						
	SR8_ZB_1820	PS- Rebar Fixing	4d	09-Feb-17	14-Feb-17					PS- Rebar Fixing						
	SR8_ZB_1830	PS- Place Concrete to Manhole Wall & Roof Slab	1d	14-Feb-17	15-Feb-17					PS- Place Concrete to Manhole Wall & Roof Slab						
	Floor Slabs & Partition Walls		14d	03-Feb-17	20-Feb-17											
	SR8_ZB_1860	PS-Internal Wall Inside Pump House	14d	03-Feb-17	20-Feb-17					PS-Internal Wall Inside Pump House						
	Remining Works inside Pump Sump E		52d	30-Dec-16	19-Feb-17											
	SR8_ZB_1890	Steel Works Installation inside Pump Sump E	45d	30-Dec-16	12-Feb-17					Steel Works Installation inside Pump Sump E						
	SR8_ZB_1900	Installation Manhole Covers for Pump Sump E	7d	13-Feb-17	19-Feb-17					Installation Manhole Covers for Pump Sump E						
	SR8 (Zone A) - Ch 317.500 to Ch 210.000 - U-Structure & Slab (Victoria Park)		37d	23-Dec-16 A	02-Feb-17											
	RC CCT & Backfill Ch317.5000 to Ch240.000		28d	23-Dec-16 A	02-Feb-17											
	Structure		28d	23-Dec-16 A	02-Feb-17											
	Utility Through		28d	23-Dec-16 A	02-Feb-17											
	SR8_ZA_1260	Zone A - Utility Trough for Zone A (CH240 to CH317)	28d	23-Dec-16 A	02-Feb-17		Zone A - Utility Trough for Zone A (CH240 to CH317)									
	SR8 Structural Slab Ch.240.000 to Ch.210.000		14d	30-Dec-16	12-Jan-17											
	SR8_2090B	Zone A - Wall - Bay 3	14d	30-Dec-16*	12-Jan-17		Zone A - Wall - Bay 3									
	Works in KD9 (Include Re-provisioning Works of KD4,KD5)		231d	10-Oct-16 A	05-Jul-17											
	External Works Under KD9		231d	14-Nov-16 A	05-Jul-17											
	Tsing Fung St - RW & Subway Extension & Toe Wall at Hing Fat St		115d	03-Dec-16 A	30-Mar-17											
	Retaining Wall + Toe Wall at Hing Fat Street		115d	03-Dec-16 A	30-Mar-17											
	Retaining Wall RW8D		115d	03-Dec-16 A	14-Mar-17											
	Bay 3(10m) to Bay 4(10m)		3d	30-Dec-16	01-Jan-17											
	RW8D_1220	RW8D (Bay 3 to Bay 4) - Sub-soil & Backfilling to Base Slab	3d	30-Dec-16	01-Jan-17		RW8D (Bay 3 to Bay 4) - Sub-soil & Backfilling to Base Slab									
	Bay 2(10m) to Bay 1(12.5m)		3d	30-Dec-16	01-Jan-17											
	RW8D_1230	RW8D(B2 to B1) - Sub-soil & Backfilling to Base	3d	30-Dec-16	01-Jan-17		RW8D(B2 to B1) - Sub-soil & Backfilling to Base									
	Re-open Hing Fat Street Footpath to Plubic (Request by VPMO)		111d	03-Dec-16 A	14-Mar-17											

Activity ID	Activity Name	Original Duration	Start	Finish												
					2016		2017									
					Dec		Jan		Feb		Mar					Apr
	A4590	Backfilling of Wall after Completion of RW8D Construction	9d	03-Dec-16 A	07-Dec-16 A	Wall after Completion of RW8D Construction										
	A4600	Reinstatement of footpath for temp open to public	9d	07-Dec-16 A	14-Dec-16 A	Reinstatement of footpath for temp open to public										
	A4610	Re-open Hing Fat Street Footpath for Plubic (From 5m CCTV footing to subway)	90d	15-Dec-16 A	14-Mar-17										Re-open Hing Fat Street Footpath for Pl	
	Works along RW8D During Reopen Hing Fat Street Footpath to Public		63d	03-Jan-17	07-Mar-17											
	A4910	Cross Road Duct to Connect C19 Cable Draw Pit at Isalnd in Tsing Fung Street	45d	03-Jan-17*	28-Feb-17										Cross Road Duct to Connect C19 Cable Draw Pit at Isalnd in Tsing f	
	A4920	Demolition of Wall Head of Existing Retaining Wall at Tsing Fung Street	14d	19-Jan-17	08-Feb-17										Demolition of Wall Head of Existing Retaining Wall at Tsing Fung Street	
	A4930	Install Steel Vechile Parapet on Wall Top from RW8D to RW8C	14d	07-Feb-17	21-Feb-17										Install Steel Vechile Parapet on Wall Top from RW8D to RW8C	
	A4940	Minor Road Works above Demolished Wall Head	14d	08-Feb-17	24-Feb-17										Minor Road Works above Demolished Wall Head	
	A4950	Realign & Provide the New Road Marking From Hing Fat Street to Tsing Fung Street	7d	25-Feb-17	07-Mar-17										Realign & Provide the New Road Marking From Hing F	
	Retaining Walls RW8E, Sign Footings & Sewer Pipe (SK266G, SK539C, SK375B)		14d	15-Mar-17	30-Mar-17											
	A4620	Excavate and lay blinding layer of RW8E	14d	15-Mar-17	30-Mar-17										Excavate	
	Foul Drain Pipe (VP Area, SK266G, SK265C & SK226L)		76d	14-Nov-16 A	21-Feb-17											
	A4480	MH2-68B to MH2-69	14d	14-Nov-16 A	12-Dec-16 A	2-68B to MH2-69										
	A4490	MH2-69 to MH2-70	14d	30-Dec-16	16-Jan-17										MH2-69 to MH2-70	
	A4440	MH2-63 to MH2-64 (under temp containers)	14d	16-Jan-17*	04-Feb-17										MH2-63 to MH2-64 (under temp containers)	
	A4460	MHA (beside pump sump E) to MH2-61	14d	04-Feb-17	21-Feb-17										MHA (beside pump sump E) to MH2-61	
	Storm Drain Pipe behind RW8C along Tsing Fung Street (SK547A)		60d	21-Nov-16 A	16-Jan-17											
	A4510	MH TFS-03 to MH TFS-04 (with gully)	14d	21-Nov-16 A	14-Dec-16 A	MH TFS-03 to MH TFS-04 (with gully)										
	A4520	MH TFS-04 to TFS-04a	11d	05-Dec-16 A	09-Dec-16 A	4 to TFS-04a										
	A4530	TFS-04a to Extg MHA1	11d	10-Dec-16 A	15-Dec-16 A	TFS-04a to Extg MHA1										
	A4540	MHTFS-05 to extg MH A3 (gully)	14d	30-Dec-16	16-Jan-17										MHTFS-05 to extg MH A3 (gully)	
	Sign Footings at Victoria Park		75d	30-Dec-16	31-Mar-17											
	A4570	Construction of 5m CCTV, AID, OHVD, TSG, luminance meter at verge inside VP	60d	30-Dec-16	14-Mar-17										Construction of 5m CCTV, AID, OHVD, T	
	A4580	All drawpits (ATC, E&M and lighting) and ductings at verge inside VP (SK375B)	60d	18-Jan-17	31-Mar-17										All draw	
	Boundary Fence, Type 2 Railing Footings & Fence Wall From RW8C to Zone B		188d	23-Dec-16 A	05-Jul-17											
	A4710	Modification of extg type 2 railing footing in front of RW8C (approx. 40m)	30d	23-Dec-16 A	14-Mar-17										Modification of extg type 2 railing footing	
	A4700	Construction of boundary fenceadjacent RW8C toe wall (approx. 40m)	30d	30-Dec-16*	07-Feb-17										Construction of boundary fenceadjacent RW8C toe wall (approx. 40m)	
	A4990	Abour Footings Construction	14d	11-Mar-17	25-Mar-17										Abour Footings Cor	
	A4720	Construction of boundary fence (approx. 460m)	90d	15-Mar-17	05-Jul-17											
	A5000	Shelter & Benches Installation	21d	25-Mar-17	15-Apr-17											
	A4730	Fence wall between BGO and Zone A (60m)	30d	24-Nov-17 A	11-Mar-17											
	Other Storm, Sewerage Pipe & Irrigation System in VP (SK336D, SK539C)		70d	04-Feb-17	04-May-17											
	A4740	FMH-B03 to Extg 1-40 (8 MHs and 7 foul pipeline)	40d	04-Feb-17	23-Mar-17										FMH-B03 to Extg 1-40	
	A4780	Complete Backfilling & Removal Top Two Layer of Strut at Bay 3 of Zone B	14d	01-Mar-17*	16-Mar-17										Complete Backfilling & Removal Top	
	A4760	MHB (beside pump sump E) to MH2-70 (300 dia. stormwater pipeline)	14d	17-Mar-17	01-Apr-17										MHB	
	A4750	SHM-B01 to Extg. MH A3 (4 MHS and 4 storm pipeline)	30d	23-Mar-17	04-May-17											
	Preparation Works before Implementation TTA at Central Median		64d	30-Dec-16	04-Mar-17											
	A4790	Construction of drawpit, ducting and remedial work on top of RW8C etc on top of RW8C	30d	30-Dec-16	07-Feb-17										Construction of drawpit, ducting and remedial work on top of RW8C etc on top of RW8C	
	A4800	Lay temp bituminous pavement for road diversion beside RW8C (Incl. Steel Vehicle Parapet on RW8C)	20d	08-Feb-17	02-Mar-17										Lay temp bituminous pavement for road diversion beside RW8C	
	A4810	Implement TTA for Closing Central Median at Tsing Fung Street	1d	03-Mar-17	04-Mar-17										Implement TTA for Closing Central Median at Tsing Fung Stre	
	Centre Median at Tsing Fung Street (SK375B, SK226L)		60d	04-Mar-17	19-May-17											
	A4820	Construct VMS6, LCS footing, ATC drawpit and ducts , steel vehicle parapet	60d	04-Mar-17	19-May-17											
	Works in Victoria Park (KD4, KD5, KD9)		153d	10-Oct-16 A	02-Jun-17											
	Re-Provisioning Works		153d	10-Oct-16 A	02-Jun-17											

Activity ID	Activity Name	Original Duration	Start	Finish										
					2016		2017							
					Dec		Jan	Feb	Mar	Apr				
Nursery Compound														
Submission														
ABWF Submission														
Material														
VP_NC_1050	ABWF Materail - ER Review and Approval	28d	18-Oct-16 A	30-Dec-16			ABWF Materail - ER Review and Approval							
VP_NC_1060	ABWF Issue P.O. / MAnufacturing / Fabrication	30d	30-Dec-16	07-Feb-17				ABWF Issue P.O. / MAnufacturing / Fabrication						
VP_NC_1070	ABWF Materail Delivery	30d	08-Feb-17	14-Mar-17					ABWF Materail Delivery					
Shop Drawing														
VP_NC_1080	ABWF Shop Drawing - Submission	21d	10-Oct-16 A	31-Dec-16			ABWF Shop Drawing - Submission							
VP_NC_1090	ABWF Shop Drawing - ER Review and Approval	60d	03-Jan-17	16-Mar-17					ABWF Shop Drawing - ER Review and Approval					
E&M Submission														
Material														
VP_NC_1130	E&M Materail - ER Review and Approval	28d	21-Oct-16 A	06-Jan-17			E&M Materail - ER Review and Approval							
VP_NC_1140	E&M Issue P.O. / MAnufacturing / Fabrication	15d	07-Jan-17	24-Jan-17			E&M Issue P.O. / MAnufacturing / Fabrication							
VP_NC_1150	E&M Materail Delivery	30d	25-Jan-17	03-Mar-17				E&M Materail Delivery						
Shop Drawing														
VP_NC_1160	E&M Shop Drawing - Submission	21d	07-Jan-17	03-Feb-17			E&M Shop Drawing - Submission							
VP_NC_1170	E&M Shop Drawing - ER Review and Approval	30d	04-Feb-17	10-Mar-17				E&M Shop Drawing - ER Review and Approval						
Nursery compound														
A4370	Backfill to ground slab and beams (including underground PE pipes installation work)	8d	24-Nov-16 A	03-Dec-16 A			and beams (including underground PE pipes installation work)							
A4380	Construction of ground slab and beams	7d	09-Dec-16 A	30-Dec-16			Construction of ground slab and beams							
A4390	Fix rebar and erect walls, columns, falsework and fwk to roof slab and beams	12d	30-Dec-16	13-Jan-17			Fix rebar and erect walls, columns, falsework and fwk to roof slab and beams							
A4400	Construction of roof slab and beams	7d	14-Jan-17	21-Jan-17			Construction of roof slab and beams							
A4410	Concreting of two concrete plinths, 150 thick curbs and 1450H parapet wall above roof slab	7d	23-Jan-17	02-Feb-17				Concreting of two concrete plinths, 150 thick curbs and 1450H parapet wall above roof slab						
A4420	ABWF, Plumbing Works, waterproofing and E&M works	60d	17-Mar-17	02-Jun-17										
Sea Wall Reinstatement & Reverting Traffic for IEC,VP Rd & TF St (KD9)														
Reinstatement Existing Slopping & Vertical Sea Wall														
Major Reinstatement Works for Seawall Reinstatement														
Stage 1														
A5040	Diversion of Temporary Pedestrian Walkway on D-wall	7d	02-Mar-17	09-Mar-17										
TTA Revert Traffic Back to Original Alignment														
Preparation Works - Backfill of Zone C to Top of Tunnel Structure														
A5780	Curing to Roof Slab of Zone C	3d	15-Feb-17	18-Feb-17										
A5790	Waterproofing & Screeding to Roof	4d	18-Feb-17	22-Feb-17										
A5800	Load Transfer for King Post	6d	22-Feb-17	28-Feb-17										
A5810	Make Good Box-out Left by King Post	2d	28-Feb-17	02-Mar-17										
A5820	Backfill to Formation & Remove Struts SL1 to SL3 (Approx. 7m)	33d	02-Mar-17	04-Apr-17										
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks														
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)														
EW_1000	Establishment Works - for Landscape Softworks and transplanted trees in Portion XIV & XV	901d	23-Feb-15 A	14-Dec-17										
KD12 - Section 7B: Portion VI & VII (Reprov. Bowling Green Area)														
EW_1010	Establishment Works - for Landscape Softworks and transplanted trees in Portion VI & VII	177d	03-Dec-15 A	30-Dec-16										
KD10 - Preservation and Protection of Trees														
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	30-Dec-16										

Activity ID	Activity Name	Original Duration	Start	Finish																
					2016				2017											
					Dec				Jan				Feb				Mar			
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)		1423d	21-Mar-13 A	30-Dec-16																
MAR_2000	Mooring Upkeep at Portion XIX(19) & XX(20) - ATS (if instructed by Engineer)	1399d	21-Mar-13 A	30-Dec-16																
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	30-Dec-16																
Works for Public Works Regional Laboratory (North Lantau) - KD1,KD16,KD17)		1301d	19-Jul-13 A	21-Nov-17																
KD17 - Maintenance and Upkeep of New PWRL (Portion XVII)		1301d	19-Jul-13 A	21-Nov-17																
PWRL_1050	Maintenance/ Upkeep of New PWRL	1301d	19-Jul-13 A	21-Nov-17																

SR8_DWP_R07-06 MU49			SR8 - Layout for 3MRP_2107_04			Appendix C.5																		
Activity ID		Activity Name		Original Duration	Start	Finish	2017																	
							Apr			May			Jun			Jul								
Total				1791d	21-Mar-13 A	09-Feb-18																		
DWP-07 - (6) - Update Progress As of 20 Apr 17				1791d	21-Mar-13 A	09-Feb-18																		
Works in KD2				95d	01-Mar-17 A	03-Jun-17																		
Works in TS3-East				95d	01-Mar-17 A	03-Jun-17																		
Removal of Temporary Reclamation at TS3(E)				95d	01-Mar-17 A	03-Jun-17																		
TS3E Remaining Works & TS3E/TS3W, TS3E/TS2 Sitiching Works				95d	01-Mar-17 A	03-Jun-17																		
West Bound Tunnel (W/B)				91d	01-Mar-17 A	30-May-17																		
Outstanding Reinforced Concrete Works				91d	01-Mar-17 A	30-May-17																		
A6570	General Cleaning Works for the Tunnel, CCTV and Pipe WaterJack Cleaning			10d	01-Mar-17 A	07-Apr-17 A	General Cleaning Works for the Tunnel, CCTV and Pipe WaterJack Cleaning																	
A6580	Joint Site Walk			5d	20-Apr-17	24-Apr-17	Joint Site Walk																	
A6590	Handover Date			1d	30-May-17	30-May-17	Handover Date																	
Stitching of TS2 & TS3E (5.0 m Tunnel Length for Base Slab, Roof Slab, Approx. 15 m length for OHVD)				40d	20-Apr-17	29-May-17																		
A6650	TS2/TS3E OHVD (Hindrance: Falsework Erection and Rebar Lifting) - 10 days			23d	20-Apr-17	12-May-17	TS2/TS3E OHVD (Hindrance: Falsework Erection and Rebar Lifting) - 10 days																	
A6660	Falsework Removal for OHVD - 7 days			7d	23-May-17	29-May-17	Falsework Removal for OHVD - 7 days																	
Profile Barrier and Maintenance Walkway				8d	20-Apr-17	27-Apr-17																		
A6700	Install Precast Concrete Covers on Cable Trough (2 X 90m)			8d	20-Apr-17	27-Apr-17	Install Precast Concrete Covers on Cable Trough (2 X 90m)																	
East Bound Tunnel (E/B)				62d	06-Mar-17 A	03-Jun-17																		
Outstanding Reinforced Concrete Works				62d	06-Mar-17 A	03-Jun-17																		
A6950	General Cleaning Works for the Tunnel			25d	11-Mar-17 A	23-Mar-17 A	General Cleaning Works for the Tunnel																	
A6960	Joint Site Walk			5d	29-May-17	02-Jun-17	Joint Site Walk																	
A6970	Handover Date			1d	03-Jun-17	03-Jun-17	Handover Date																	
Stitching of TS2 & TS3E (5.0 m Length for Base Slab, Roof Slab, Approx. 15 m length for OHVD)				56d	06-Mar-17 A	28-May-17																		
A6860	TS2/TS3E OHVD (Hindrance: Falsework Erection and Rebar Lifting) - 10 days			10d	06-Mar-17 A	11-May-17	TS2/TS3E OHVD (Hindrance: Falsework Erection and Rebar Lifting) - 10 days																	
A6870	Falsework Removal for OHVD - 7 days			7d	22-May-17	28-May-17	Falsework Removal for OHVD - 7 days																	
Profile Barrier and Maintenance Walkway				8d	24-Mar-17 A	31-Mar-17 A																		
A6910	Install Precast Concrete Covers on Cable Trough (2 X 90m)			8d	24-Mar-17 A	31-Mar-17 A	Install Precast Concrete Covers on Cable Trough (2 X 90m)																	
Works in KD7				81d	04-Mar-17 A	08-Jun-17																		
Works in TS3-West				81d	04-Mar-17 A	08-Jun-17																		
Tunnel Structure				81d	04-Mar-17 A	08-Jun-17																		
Earthwork Backfilling, ELS Removal and Water Recharging				38d	04-Mar-17 A	06-Apr-17 A																		
East Portion				38d	04-Mar-17 A	30-Mar-17 A																		
A2490	Stage 4 Backfilling- 25000 m3 (~14mPD~ -7.0 mPD, Bay 2- Bay 4) - 1000 m3 per day			19d	04-Mar-17 A	22-Mar-17 A	Stage 4 Backfilling- 25000 m3 (~14mPD~ -7.0 mPD, Bay 2- Bay 4) - 1000 m3 per day																	
A2520	Stage 5 Backfilling ~ 15000 m3 (~30 mPD ~ -7.0 mPD, Bay 1) ~ 1000 m3 per day			10d	22-Mar-17 A	28-Mar-17 A	Stage 5 Backfilling ~ 15000 m3 (~30 mPD ~ -7.0 mPD, Bay 1) ~ 1000 m3 per day																	
A2500	Removal of 2nd Layer ELS and Removal of Reprop inside Tunnel (Bay 2- Bay 4)			7d	23-Mar-17 A	26-Mar-17 A	Removal of 2nd Layer ELS and Removal of Reprop inside Tunnel (Bay 2- Bay 4)																	
A2510	Closure of wall opening in Bay 1 of CCT (Wall 4 and Wall 5)			14d	23-Mar-17 A	26-Mar-17 A	Closure of wall opening in Bay 1 of CCT (Wall 4 and Wall 5)																	
A2530	Removal of 2nd Layer ELS (Bay 1)			5d	29-Mar-17 A	30-Mar-17 A	Removal of 2nd Layer ELS (Bay 1)																	
West Portion				6d	10-Mar-17 A	20-Mar-17 A																		
A2550	Removal of 2nd Layer ELS - 6 days			6d	10-Mar-17 A	20-Mar-17 A	Removal of 2nd Layer ELS - 6 days																	
Water Recharge (CNY- 27/1~ 2/2)				1d	31-Mar-17 A	06-Apr-17 A																		
A2560	Water Re-charge to ELS Cofferdam			1d	31-Mar-17 A	06-Apr-17 A	Water Re-charge to ELS Cofferdam																	
Skin Wall Removal Works between TS4/TS3W and Shaft D Closure				81d	23-Mar-17 A	08-Jun-17																		
A2590	Skin Wall Removal Works between TS4/TS3W - 20 days (2nd stage) - After Tunnel Roof Slab Completion - E/B and W/B			20d	23-Mar-17 A	09-May-17	Skin Wall Removal Works between TS4/TS3W - 20 days (2nd stage) - After Tunnel Roof Slab Completion - E/B and W/B																	
A2600	Construction of Remaining Tunnel Structure between CH. 4260.2- 4265.2 at SOL T100 for Mainline E/B, W/B, SR8			30d	10-May-17	08-Jun-17	Construction of Remaining Tunnel Structure between CH. 4260.2- 4265.2 at SOL T100 for Mainline E/B, W/B, SR8																	
				Actual Work		Remaining Work		Critical Remaining Work		Milestone		Page 1 of 8					Date		Revision		Checked		Approved	
												Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Progamme					20-Apr-17		DWP-07 (6) - 3 Months Rolling		FS		TL	

Activity ID		Activity Name	Original Duration	Start	Finish	2017											
						Apr			May			Jun			Jul		
		Removal Bulkhead at CH525 (TS3W / SR8 Junction)	41d	06-Mar-17 A	13-Apr-17 A												
A6080		Remove Bulkhead between TS3W & SR8	37d	06-Mar-17 A	13-Apr-17 A	Remove Bulkhead between TS3W & SR8											
A5180		Remove Scaffolding of SR1R Roof	4d	22-Mar-17 A	25-Mar-17 A	of SR1R Roof											
Works in KD8			129d	09-Mar-17 A	28-Jul-17												
TS3W - Remove Temporary Reclamation			129d	09-Mar-17 A	28-Jul-17												
Stage 1 - North West Corner (Bay Z4-25 to Bay 20)			56d	09-Mar-17 A	14-Apr-17 A												
A2660		Remove filled material to -4.35mPD at Bay Z4-25 to Bay 19 (6,500m3)	8d	09-Mar-17 A	24-Mar-17 A	l to -4.35mPD at Bay Z4-25 to Bay 19 (6,500m3)											
A2670		Remove filled material to -4.35mPD at Bay Z4-22 to Z4-24 (4,500m3)	5d	25-Mar-17 A	14-Apr-17 A	Remove filled material to -4.35mPD at Bay Z4-22 to Z4-24 (4,500m3)											
A2680		Remove seawall blocks at Bay Z4-25 to Bay 20 (426 nos.)	8d	27-Mar-17 A	10-Apr-17 A	Remove seawall blocks at Bay Z4-25 to Bay 20 (426 nos.)											
A6260		Remove filled material to -7.0 mPD	4d	05-Apr-17 A	13-Apr-17 A	Remove filled material to -7.0 mPD											
Stage 2 - North to East Side (Bay 19 to Bay 11 + Bay 26 to Bay 28)			14d	24-Mar-17 A	07-Apr-17 A												
A2690		Break concrete slab at Bay 19 to Bay 11 + Bay 26 to Bay 28 (2,500m2)	7d	24-Mar-17 A	31-Mar-17 A	concrete slab at Bay 19 to Bay 11 + Bay 26 to Bay 28 (2,500m2)											
A2700		Remove filled material to +2.8mPD (2,500m3)	7d	01-Apr-17 A	07-Apr-17 A	Remove filled material to +2.8mPD (2,500m3)											
Stage 3 - North to East Side (Bay 19 to bay 26)			49d	31-Mar-17 A	01-May-17												
A2710		Completion of Recharging of Sea Water into TS3W Cofferdam	2d	31-Mar-17 A	04-Apr-17 A	Completion of Recharging of Sea Water into TS3W Cofferdam											
North West D-wall Opening			22d	07-Apr-17 A	29-Apr-17 A												
A2720		Core D-wall cut holes at Panel DW02 to NA6 (27 nos.)	6d	07-Apr-17 A	10-Apr-17 A	Core D-wall cut holes at Panel DW02 to NA6 (27 nos.)											
A2730		Vertical cut at Panel DW02 to NA6 (19 nos.)	8d	14-Apr-17 A	20-Apr-17 A	Vertical cut at Panel DW02 to NA6 (19 nos.)											
A2740		Horizontal cut at Panel DW02 to NA6 (25 nos.)	8d	21-Apr-17 A	29-Apr-17 A	Horizontal cut at Panel DW02 to NA6 (25 nos.)											
North East & East			13d	13-Apr-17 A	01-May-17												
A2750		Remove filled material to -4.35mPD (22,500m3)	9d	13-Apr-17 A	26-Apr-17	Remove filled material to -4.35mPD (22,500m3)											
A2760		Remove seawall blocks at Bay 19 to 11 & Bay 26 to 28 (1,335 nos.)	13d	20-Apr-17 A	29-Apr-17	Remove seawall blocks at Bay 19 to 11 & Bay 26 to 28 (1,335 nos.)											
A2770		Remove filled material to -7.0mPD (North & East side)	10d	29-Apr-17 A	01-May-17	Remove filled material to -7.0mPD (North & East side)											
Stage 4 - West & South Side (Remove Seawall Block Bay Z4-23 & 24, Excavate to -4.35mPD)			47d	31-Mar-17 A	05-Jun-17												
West Side			18d	31-Mar-17 A	07-May-17												
A2790		Remove seawall blocks at Bay Bay Z4-23 to Z4-24 (249 nos.)	5d	31-Mar-17 A	02-May-17	Remove seawall blocks at Bay Bay Z4-23 to Z4-24 (249 nos.)											
A2800		Remove filled material to -7.0mPD (West)	5d	03-May-17	07-May-17	Remove filled material to -7.0mPD (West)											
North East Side			32d	19-Apr-17 A	05-Jun-17												
A2810		Core D-wall cut holes at Panel W1D1 to W1D32 (128 nos.) (North Side)	14d	19-Apr-17 A	26-Apr-17 A	Core D-wall cut holes at Panel W1D1 to W1D32 (128 nos.) (North Side)											
A2820		Vertical cut at Panel W1D1 to W1D32 (96 nos.) (North Side)	16d	27-Apr-17 A	08-May-17	Vertical cut at Panel W1D1 to W1D32 (96 nos.) (North Side)											
A2830		Horizontal cut at Panel W1D1 to W1D32 (128 nos.) (North Side)	20d	17-May-17	05-Jun-17	Horizontal cut at Panel W1D1 to W1D32 (128 nos.) (North Side)											
East Side			33d	20-Apr-17 A	03-Jun-17												
A2840		Core D-wall cut holes at Panel TZ31 to TZ38 (32 nos.) (East Side)	10d	20-Apr-17 A	26-Apr-17 A	Core D-wall cut holes at Panel TZ31 to TZ38 (32 nos.) (East Side)											
A2850		Vertical cut at Panel TZ31 to TZ38 (24 nos.) (East Side)	9d	16-May-17	24-May-17	Vertical cut at Panel TZ31 to TZ38 (24 nos.) (East Side)											
A2860		Horizontal cut at Panel TZ31 to TZ38 (32 nos.) (East Side)	10d	25-May-17	03-Jun-17	Horizontal cut at Panel TZ31 to TZ38 (32 nos.) (East Side)											
South Side			30d	20-Apr-17	19-May-17												
A2870		Remove filled material to -4.35mPD (41,300m3)	30d	20-Apr-17	19-May-17	Remove filled material to -4.35mPD (41,300m3)											
Stage 5 - West & South side (Reove Seawwall Block Bay 24 7 25, Excvavate to -7.0mPD)			30d	12-Apr-17 A	06-Jun-17												
A2910		Core D-wall cut holes at Panel BWD2 to BWD9 (30 nos.) (West Side)	5d	12-Apr-17 A	17-Apr-17 A	Core D-wall cut holes at Panel BWD2 to BWD9 (30 nos.) (West Side)											
A2920		Vertical cut at Panel BWD2 to BWD9 (22 nos.) (West Side)	8d	08-May-17	15-May-17	Vertical cut at Panel BWD2 to BWD9 (22 nos.) (West Side)											
A2930		Horizontal cut at Panel BWD2 to BWD9 (29 nos.) (West Side)	8d	16-May-17	23-May-17	Horizontal cut at Panel BWD2 to BWD9 (29 nos.) (West Side)											
A2880		Remove seawall blocks at Bay 24, 25 (264 nos.) (South West)	6d	20-May-17	25-May-17	Remove seawall blocks at Bay 24, 25 (264 nos.) (South West)											
A2890		Remove seawall blocks at Bay 2 to 4 (550 nos.) (South East)	11d	20-May-17	30-May-17	Remove seawall blocks at Bay 2 to 4 (550 nos.) (South East)											
A2900		Remove filled material to -7.0mPD (South)	7d	31-May-17	06-Jun-17	Remove filled material to -7.0mPD (South)											



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 2 of 8

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip
Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2017														
					Apr			May			Jun			Jul					
Stage 6 - West & South Side (Saw Cut D-wall + Shaft D)					48d	24-May-17	10-Jul-17												
A2940	Remove fill material to -7.0mPD around shaft D	5d	24-May-17	28-May-17															
A2950	Core D-wall cut holes at PanelW2D1 to W2D18 (72 nos.) (South West)	9d	07-Jun-17	15-Jun-17															
A2980	Core D-wall cut holes at Panel W2D23 to W2D34 (50 nos.) (South East)	10d	07-Jun-17	16-Jun-17															
A2990	Vertical cut at Panel W2D23 to W2D34 (38 nos.) (South East)	13d	11-Jun-17	23-Jun-17															
A2960	Vertical cut at Panel W2D1 to W2D18 (54 nos.) (South West)	18d	15-Jun-17	02-Jul-17															
A3000	Horizontal cut at Panel W2D23 to W2D34 (50 nos.) (South East)	13d	18-Jun-17	30-Jun-17															
A2970	Horizontal cut at Panel W2D1 to W2D18 (72 nos.) (South West)	18d	23-Jun-17	10-Jul-17															
Stage 7 - West & South Side (Saw Cut Shaft D, Excavate to -7.0mPD at SR8)					40d	29-May-17	07-Jul-17												
A3010	Vertical cut at Shaft D (14 nos.)	10d	29-May-17	07-Jun-17															
A3020	Horizontal cut at Shaft D (14 nos.)	5d	08-Jun-17	12-Jun-17															
A3030	Remove filled material to -7.0mPD at SR8	7d	01-Jul-17	07-Jul-17															
Stage 8 - South East & West Side (Remove Seawall Block Bay Z4-22 to Bay 23, Saw Cut D-wall at SR8)					46d	13-Jun-17	28-Jul-17												
South West Side					42d	13-Jun-17	24-Jul-17												
A3040	Remove seawall blocks at Bay Z4-22 to Bay 23 (741 nos.)	15d	13-Jun-17	27-Jun-17															
A3050	Remove filled material to -7.0mPD (South West)	8d	28-Jun-17	05-Jul-17															
A3060	Vertical cut at Panel BWD10 to SA7 (26 nos.) (South West)	9d	06-Jul-17	14-Jul-17															
A3070	Horizontal cut at Panel BWD10 to SA7 (37 nos.) (South West)	10d	15-Jul-17	24-Jul-17															
SR08 - West Wall					21d	08-Jul-17	28-Jul-17												
A3080	Vertical cut at Panel W4D1 to W4D11 (28 nos.) (SR8)	10d	08-Jul-17	17-Jul-17															
A3090	Horizontal cut at Panel W4D1 to W4D11 (39 nos.) (SR8)	11d	18-Jul-17	28-Jul-17															
SR08 - East Wall					19d	08-Jul-17	26-Jul-17												
A7010	Vertical cut at Panel W4D1 to W4D11 (26 nos.)	9d	08-Jul-17	16-Jul-17															
A7020	Horizontal cut at Panel W3D1 to W3D7 (36 nos.)	10d	17-Jul-17	26-Jul-17															
Works in KD6					136d	22-Jan-17 A	05-Jul-17												
Works in SR8 (Open Cut Method)					136d	22-Jan-17 A	05-Jul-17												
SR8 (Zone C) - Ch. 528 to Ch. 368					88d	14-Feb-17 A	16-May-17												
Zone C - Tunnel Structure					88d	14-Feb-17 A	16-May-17												
1.2m Thick Base Slab					2d	26-Feb-17 A	21-Apr-17												
Bay C6					2d	26-Feb-17 A	21-Apr-17												
A7540	C6 - Remove Strut SL5 & SL3	2d	26-Feb-17 A	21-Apr-17															
1.0m Thick Wall at Both Side					7d	22-Apr-17	28-Apr-17												
LHS Wall					7d	22-Apr-17	28-Apr-17												
A7340	5th Pour - CH500 to CH525	7d	22-Apr-17	28-Apr-17															
200mm Thick OHVD Slab & 400mm Thick Hanger Wall					9d	01-May-17	09-May-17												
Bay C6					9d	01-May-17	09-May-17												
A7570	C6 - Construct OHVD Slab & Hanger Wall	9d	01-May-17	09-May-17															
1.2m Thick Roof Slab					55d	14-Feb-17 A	08-May-17												
Bay C4					13d	14-Feb-17 A	24-Mar-17 A												
A7610	C4 - Roof Slab Construction	13d	14-Feb-17 A	24-Mar-17 A															
Bay C5					8d	16-Mar-17 A	25-Mar-17 A												
A7620	C5 - Roof Slab Construction	8d	16-Mar-17 A	25-Mar-17 A															
Bay C6					9d	23-Mar-17 A	08-May-17												
A7630	C6 - Partial Roof + Up Stand Wall Construction for Access Shaft	9d	23-Mar-17 A	08-May-17															



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 3 of 8

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip
Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

Activity ID		Activity Name		Original Duration	Start	Finish	2017											
							Apr			May			Jun			Jul		
		Egress Passage - EP01		31d	13-Mar-17 A	24-Apr-17 A												
		Bay C1		31d	13-Mar-17 A	14-Apr-17 A												
A7690	C1 - EP01 Wall Construction	9d	13-Mar-17 A	30-Mar-17 A	Wall Construction													
A7700	C1 - EP01 Roof Construction	8d	13-Mar-17 A	30-Mar-17 A	Roof Construction													
A8010	C1 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing	14d	31-Mar-17 A	14-Apr-17 A	C1 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing													
		Bay C2		31d	13-Mar-17 A	14-Apr-17 A												
A7710	C2 - EP01 Wall Construction	9d	13-Mar-17 A	30-Mar-17 A	Wall Construction													
A7720	C2 - EP01 Roof Construction	8d	13-Mar-17 A	30-Mar-17 A	Roof Construction													
A8020	C2 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing	14d	31-Mar-17 A	14-Apr-17 A	C2 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing													
		Bay C3		31d	20-Mar-17 A	24-Apr-17 A												
A7730	C3 - EP01 Wall Construction	9d	20-Mar-17 A	05-Apr-17 A	C3 - EP01 Wall Construction													
A7740	C3 - EP01 Roof Construction	8d	20-Mar-17 A	05-Apr-17 A	C3 - EP01 Roof Construction													
A8030	C3 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing	14d	06-Apr-17 A	24-Apr-17 A	C3 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing													
		Bay C4		31d	20-Mar-17 A	24-Apr-17 A												
A7750	C4 - EP01 Wall Construction	9d	20-Mar-17 A	05-Apr-17 A	C4 - EP01 Wall Construction													
A7760	C4 - EP01 Roof Construction	8d	20-Mar-17 A	05-Apr-17 A	C4 - EP01 Roof Construction													
A8040	C4 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing	14d	06-Apr-17 A	24-Apr-17 A	C4 - Dismantle Scaffolding of EP01 Roof Slab - 10 days Curing													
		Utility Trough		27d	20-Apr-17	16-May-17												
		Bay C1		16d	20-Apr-17	05-May-17												
A7790	RHS / C1 - Backing Concrete	4d	20-Apr-17	23-Apr-17	RHS / C1 - Backing Concrete													
A7800	RHS / C1 - Profile Barrier	4d	24-Apr-17	27-Apr-17	RHS / C1 - Profile Barrier													
A7770	LHS / C1 - Backing Concrete	4d	28-Apr-17	01-May-17	LHS / C1 - Backing Concrete													
A7780	LHS / C1 - Profile Barrier	4d	02-May-17	05-May-17	LHS / C1 - Profile Barrier													
		Bay C2		16d	20-Apr-17	05-May-17												
A7830	RHS / C2 - Backing Concrete	4d	20-Apr-17	23-Apr-17	RHS / C2 - Backing Concrete													
A7840	RHS / C2 - Profile Barrier	4d	24-Apr-17	27-Apr-17	RHS / C2 - Profile Barrier													
A7810	LHS / C2 - Backing Concrete	4d	28-Apr-17	01-May-17	LHS / C2 - Backing Concrete													
A7820	LHS / C2 - Profile Barrier	4d	02-May-17	05-May-17	LHS / C2 - Profile Barrier													
		Bay C3		16d	20-Apr-17	05-May-17												
A7870	RHS / C3 - Backing Concrete	4d	20-Apr-17	23-Apr-17	RHS / C3 - Backing Concrete													
A7880	RHS / C3 - Profile Barrier	4d	24-Apr-17	27-Apr-17	RHS / C3 - Profile Barrier													
A7850	LHS / C3 - Backing Concrete	4d	28-Apr-17	01-May-17	LHS / C3 - Backing Concrete													
A7860	LHS / C3 - Profile Barrier	4d	02-May-17	05-May-17	LHS / C3 - Profile Barrier													
		Bay C4		16d	20-Apr-17	05-May-17												
A7910	RHS / C4 - Backing Concrete	4d	20-Apr-17	23-Apr-17	RHS / C4 - Backing Concrete													
A7920	RHS / C4 - Profile Barrier	4d	24-Apr-17	27-Apr-17	RHS / C4 - Profile Barrier													
A7890	LHS / C4 - Backing Concrete	4d	28-Apr-17	01-May-17	LHS / C4 - Backing Concrete													
A7900	LHS / C4 - Profile Barrier	4d	02-May-17	05-May-17	LHS / C4 - Profile Barrier													
		Bay C5		16d	01-May-17	16-May-17												
A7950	RHS / C5 - Backing Concrete	4d	01-May-17	04-May-17	RHS / C5 - Backing Concrete													
A7960	RHS / C5 - Profile Barrier	4d	05-May-17	08-May-17	RHS / C5 - Profile Barrier													
A7930	LHS / C5 - Backing Concrete	4d	09-May-17	12-May-17	LHS / C5 - Backing Concrete													
A7940	LHS / C5 - Profile Barrier	4d	13-May-17	16-May-17	LHS / C5 - Profile Barrier													
		SR8 (Zone B) - Ch.385.000 to Ch.317.500 - (Inside Victoria Park to Tunnel Portal)		77d	20-Apr-17	05-Jul-17												



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

Activity ID		Activity Name		Original Duration	Start	Finish	2017											
							Apr			May			Jun			Jul		
		SR8 (Zone B) Tunnel - ELS / CCT / BF Works (7 Bays Ch. 385.000 to Ch.317.500)		77d	20-Apr-17	05-Jul-17												
		Portal Structure		77d	20-Apr-17	05-Jul-17												
		OHVD		43d	20-Apr-17	01-Jun-17												
		Bay B1 + B2 (CH338.625 to CH368)		43d	20-Apr-17	01-Jun-17												
	SR8_ZB_1390	Zone B - OHVD - Erect Scaffolding & Soffit Formwork		6d	20-Apr-17	25-Apr-17												
	SR8_ZB_1400	Zone B - Redrill & Install Rebar on Soffit of Roof Slab		10d	26-Apr-17	05-May-17												
	SR8_ZB_1420	Zone B - OHVD - Rebar Fixing for Slab & Hanger Wall of OHVD		4d	06-May-17	10-May-17												
	SR8_ZB_1430	Zone B - OHVD Erect Hanger Wall Formwork for OHVD		2d	11-May-17	12-May-17												
	SR8_ZB_1440	Zone B - OHVD Place Concrete to OHVD Slab & Wall		1d	13-May-17	13-May-17												
	SR8_ZB_1450	Zone B - OHVD Curing Period for OHVD Slab		10d	15-May-17	25-May-17												
	SR8_ZB_1460	Zone B - OHVD Remove Soffit Formwork & Scaffolding		5d	26-May-17	01-Jun-17												
		Utility Trough		28d	02-Jun-17	05-Jul-17												
		Left Hand Side		21d	10-Jun-17	05-Jul-17												
	SR8_ZB_1570	Zone B - U trough (LHS) Bay 3		7d	10-Jun-17	17-Jun-17												
	SR8_ZB_1560	Zone B - U trough (LHS) Bay 2		7d	19-Jun-17	26-Jun-17												
	SR8_ZB_1550	Zone B - U trough (LHS) Bay 1		7d	27-Jun-17	05-Jul-17												
		Right Hand Side		21d	02-Jun-17	26-Jun-17												
	SR8_ZB_1600	Zone B - U trough (RHS) Bay 3		7d	02-Jun-17	09-Jun-17												
	SR8_ZB_1590	Zone B - U trough (RHS) Bay 2		7d	10-Jun-17	17-Jun-17												
	SR8_ZB_1580	Zone B - U trough (RHS) Bay 1		7d	19-Jun-17	26-Jun-17												
		Pump House		52d	20-Apr-17	10-Jun-17												
		Remining Works inside Pump Sump E		52d	20-Apr-17	10-Jun-17												
	SR8_ZB_1890	Steel Works Installation inside Pump Sump E		45d	20-Apr-17	03-Jun-17												
	SR8_ZB_1900	Installation Manhole Covers for Pump Sump E		7d	04-Jun-17	10-Jun-17												
		SR8 (Zone A) - Ch 317.500 to Ch 210.000 - U-Structure & Slab (Victoria Park)		28d	22-Jan-17 A	26-May-17												
		RC CCT & Backfill Ch317.5000 to Ch240.000		28d	22-Jan-17 A	26-May-17												
		Structure		28d	22-Jan-17 A	26-May-17												
		Utility Through		28d	22-Jan-17 A	26-May-17												
	SR8_ZA_1260	Zone A - Utility Trough for Zone A (CH240 to CH317)		28d	22-Jan-17 A	26-May-17												
		Works in KD9 (Include Re-provisioning Works of KD4,KD5)		299d	12-Dec-16 A	11-Sep-17												
		External Works Under KD9		299d	12-Dec-16 A	11-Sep-17												
		Tsing Fung St - RW & Subway Extension & Toe Wall at Hing Fat St		191d	23-Jan-17 A	01-Aug-17												
		Retaining Wall + Toe Wall at Hing Fat Street		191d	23-Jan-17 A	01-Aug-17												
		Retaining Wall RW8D		100d	23-Jan-17 A	02-May-17												
		Bay 3(10m) to Bay 4(10m)		6d	23-Jan-17 A	23-Mar-17 A												
	RW8D_1220	RW8D (Bay 3 to Bay 4) - Sub-soil &Backfilling to Base Slab		6d	23-Jan-17 A	23-Mar-17 A												
		Works along RW8D During Reopen Hing Fat Street Footpath to Public		33d	01-Mar-17 A	02-May-17												
	A4910	Close slow lane of HFS to cut coping of RW8D and subway		20d	01-Mar-17 A	26-Apr-17 A												
	A4920	Lay temp bituminous pavement for road diversion (from RW8D to Subway)		3d	20-Apr-17	22-Apr-17												
	A4940	Install steel vehicle parapet on RW8C, subway and RW8D		10d	20-Apr-17	02-May-17												
		Retaining Walls RW8E, Sign Footings & Sewer Pipe (SK266G, SK539C, SK375B)		135d	20-Mar-17 A	01-Aug-17												
	A4615	Re-occupy Hing Fat Street Footpath as site Area		1d	20-Mar-17 A	20-Mar-17 A												
	A4620	Excavate and lay blinding layer of RW8E (Including ELS)		14d	19-Apr-17 A	08-May-17												
	A4880	DS16 - Sign Frame Installation		14d	20-Apr-17	03-May-17												



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

Activity ID	Activity Name	Original Duration	Start	Finish	2017											
					Apr			May			Jun			Jul		
A4650	MH2-70 to MH2-71(150 dia. foul sewer pipe)	12d	20-Apr-17	05-May-17						MH2-70 to MH2-71(150 dia. foul sewer pipe)						
A4630	Construction of RW8E and toe wall (2+1 bays, 32m long)	45d	09-May-17	30-Jun-17											Construction of RW8E and toe wall (2+1 bays, 32m long)	
A4640	Backfill and subsoil drainage system behind RW8E	14d	03-Jul-17	18-Jul-17											Backfill and subsoil drainage system behind RW8E	
A4670	MH2-72 to MH2-73	12d	19-Jul-17	01-Aug-17												
Storm Drain Pipe behind RW8C along Tsing Fung Street (SK547A)		42d	20-Apr-17	10-Jun-17												
A4540	Modified MH shaft A2 at extg box culvert near MH TFS-04A	14d	20-Apr-17*	08-May-17						Modified MH shaft A2 at extg box culvert near MH TFS-04A						
A6410	MHTFS-06 to extg MH A3 (at slow lane of TFS)	14d	09-May-17	24-May-17						MHTFS-06 to extg MH A3 (at slow lane of TFS)						
A8050	MHTFS-05 to extg MH A3 (gully)	14d	25-May-17	10-Jun-17											MHTFS-05 to extg MH A3 (gully)	
Sign Footings at Victoria Park		75d	20-Apr-17	20-Jul-17												
A4570	Construction of 5m CCTV, AID, OHVD, TSG, luminance meter at verge inside VP	60d	20-Apr-17*	03-Jul-17											Construction of 5m CCTV, AID, OHVD, TSG, luminance meter at verge inside VP	
A4580	All drawpits (ATC, E&M and lighting) and ductings at verge inside VP (SK375B)	60d	10-May-17	20-Jul-17											All drawpits (ATC, E&M and lighting) and ductings at verge inside VP (SK375B)	
Boundary Fence, Type 2 Railing Footings & Fence Wall From RW8C to Zone B		242d	12-Dec-16 A	11-Sep-17												
A8070	Fence wall between BGO and Zone A (78.2m)	90d	12-Dec-16 A	03-Jul-17											Fence wall between BGO and Zone A (78.2m)	
A4700	Construction of boundary fence from RW8C toe wall to 15m CCTV high mast (approx. 53m)	50d	19-Dec-16 A	20-May-17						Construction of boundary fence from RW8C toe wall to 15m CCTV high mast (approx. 53m)						
A4710	Modification/ Re-construction of extg type 2 railing footing in front of RW8C (approx. 40m)	60d	10-Feb-17 A	01-Aug-17												
A4720	Construction of boundary fence from 15m CCTV high mast to Zone A at CH210 (approx. 50m)	50d	22-May-17	20-Jul-17											Construction of boundary fence from 15m CCTV high mast to Zone A at CH210 (approx. 50m)	
A4730	Construction of boundary fence near nursery compound (approx. 167m, after completion of MH 2-73)	90d	27-May-17	11-Sep-17												
Other Storm, Sewerage Pipe & Irrigation System in VP (SK336E, SK539D)		141d	21-Feb-17 A	07-Aug-17												
A4770	MH2-71 to TFS-06 via MH2-72 and MH 2-73 (300 dia. concrete pipe)	40d	21-Feb-17 A	26-May-17						MH2-71 to TFS-06 via MH2-72 and MH 2-73 (300 dia. concrete pipe)						
A4740	FMH-B01 to Extg 1-40 (5 MHs and 7 foul sewer PE pipeline)	90d	20-Apr-17	07-Aug-17												
A4970	Irrigation Main Laying	14d	27-May-17	09-Jun-17											Irrigation Main Laying	
A4760	MHB (beside pump sump E) to MH2-70 (300 dia. stormwater pipeline)	14d	27-May-17	13-Jun-17											MHB (beside pump sump E) to MH2-70 (300 dia. stormwater pipeline)	
A4980	Water Points Installation	14d	10-Jun-17	23-Jun-17											Water Points Installation	
Preparation Works before Implementation TTA at Central Median		141d	02-Feb-17 A	20-Jul-17												
A4795	Excavate to formation level and lay subbase, fix K1 kerb along TFS	14d	02-Feb-17 A	05-May-17						Excavate to formation level and lay subbase, fix K1 kerb along TFS						
A4890	Laying Ducting Cross Access Ramp Down to Zone C SR8 Tunnel	60d	20-Apr-17	18-Jun-17											Laying Ducting Cross Access Ramp Down to Zone C SR8 Tunnel	
A4930	Shifting Site Entrance 6A	4d	19-Jun-17	22-Jun-17											Shifting Site Entrance 6A	
A4950	Laying Ducting in New SR8 Approaching Island	14d	23-Jun-17	06-Jul-17											Laying Ducting in New SR8 Approaching Island	
A5020	Forming Island Including Sub-base & Kerbing	14d	07-Jul-17	20-Jul-17											Forming Island Including Sub-base & Kerbing	
Reverting Traffic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)		98d	27-Mar-17 A	13-Aug-17												
TTA Revert Traffic Back to Original Alignment		98d	27-Mar-17 A	13-Aug-17												
Preparation Works - Backfill of Zone C to Top of Tunnel Structure		59d	27-Mar-17 A	16-Jun-17												
A5790	Waterproofing & Screeding to Roof	4d	27-Mar-17 A	14-May-17						Waterproofing & Screeding to Roof						
A5800	Load Transfer for King Post	6d	05-Apr-17 A	20-May-17						Load Transfer for King Post						
A5820	Zone C - Bay C1 to C5 Backfill to Formation & Remove Struts SL1 to SL3 (Up to +2.5mPD)	44d	10-Apr-17 A	16-Jun-17											Zone C - Bay C1 to C5 Backfill to Formation & Remove Struts SL1 to SL3 (Up to +2.5mPD)	
A5780	Curing to Roof Slab of Zone C	3d	08-May-17	10-May-17						Curing to Roof Slab of Zone C						
A5810	Make Good Box-out Left by King Post	2d	21-May-17	22-May-17						Make Good Box-out Left by King Post						
East Bound TTA - IEC East Bound, Victoria Park Road & Footpath along Sea Side		30d	17-Jun-17	16-Jul-17												
Stage 1 - IEC (East Bound)		30d	17-Jun-17	16-Jul-17												
A5240	IEC/EB - Construct Footing of Sign Gantry & Wing Wall	17d	17-Jun-17	03-Jul-17											IEC/EB - Construct Footing of Sign Gantry & Wing Wall	
A5260	IEC/EB - Backfill to Formation Level (Approx. 2.2mPD to +3.9mPD)	5d	17-Jun-17	21-Jun-17											IEC/EB - Backfill to Formation Level (Approx. 2.2mPD to +3.9mPD)	
A5270	IEC/EB - Reconstruct Wing Wall of Abutment M (approx. 6m)	10d	17-Jun-17	26-Jun-17											IEC/EB - Reconstruct Wing Wall of Abutment M (approx. 6m)	
A5280	IEC/EB - Cast Central Median	21d	17-Jun-17	07-Jul-17											IEC/EB - Cast Central Median	
A5310	IEC/EB - Remove Temporary Utilities Supports at IEC	3d	17-Jun-17	19-Jun-17											IEC/EB - Remove Temporary Utilities Supports at IEC	

Activity ID		Activity Name	Original Duration	Start	Finish	2017											
						Apr			May			Jun			Jul		
	A3285	IEC/EB - Cut and Remove Pipe Pile (2m Below Ground Level)	7d	17-Jun-17	23-Jun-17												IEC/EB - Cut and Remove Pipe Pile (2m Below Ground Level)
	A5320	IEC/EB - Reinstate Existing Drainage System	14d	20-Jun-17	03-Jul-17												IEC/EB - Reinstate Existing Drainage Syst
	A3286	IEC/EB - Cut and Remove Sheet Pile (2m Below Ground Level)	7d	24-Jun-17	30-Jun-17												IEC/EB - Cut and Remove Sheet Pile (2m Below
	A5290	IEC/EB - Street Lighting Cable Duct & Poles	3d	01-Jul-17	03-Jul-17												IEC/EB - Street Lighting Cable Duct & Pole
	A5250	IEC/EB - Install A Frame of Sign Gantry	4d	04-Jul-17	07-Jul-17												IEC/EB - Install A Frame of Sign G
	A5300	IEC/EB - TOC of Street Lightings	2d	04-Jul-17	05-Jul-17												IEC/EB - TOC of Street Lightings
	A5330	IEC/EB - Backfill Drainage Tranch Up to Formnation (+2.5mPd to +3.9mPD)	5d	04-Jul-17	08-Jul-17												IEC/EB - Backfill Drainage Tranc
	A5340	IEC/EB - Laying Sub-base	2d	09-Jul-17	10-Jul-17												IEC/EB - Laying Sub-base
	A5350	IEC/EB - Laying Asphlat Pavement	3d	11-Jul-17	13-Jul-17												IEC/EB - Laying Asphla
	A5360	IEC/EB - Road Mark & Traffic Signs	3d	14-Jul-17	16-Jul-17												IEC/EB - Road M
West Bound - IEC West Bound & Tsing Fung Street			58d	17-Jun-17	13-Aug-17												
Stage 1 - IEC (West Bound)			30d	17-Jun-17	16-Jul-17												
	A5690	IEC/WB - Cut pipe pile - 1 week	7d	17-Jun-17	23-Jun-17												IEC/WB - Cut pipe pile - 1 week
	A5710	IEC/WB - Removal of pedestrian decking	11d	17-Jun-17	27-Jun-17												IEC/WB - Removal of pedestrian decking
	A3785	IEC/WB - Reconstruct Wing Wall of Abutment M (approx. 6m)	10d	17-Jun-17	26-Jun-17												IEC/WB - Reconstruct Wing Wall of Abutment M (approx
	A5700	IEC/WB - Cut sheetpile - 1 week	7d	24-Jun-17	30-Jun-17												IEC/WB - Cut sheetpile - 1 week
	A5720	IEC/WB - Remove temporary utilities support 3 days	3d	28-Jun-17	30-Jun-17												IEC/WB - Remove temporary utilities support 3
	A5730	IEC/WB - Backfill up to Formation under Asphalt (from +2.5mPD to +3.9mPD) 5 days	5d	01-Jul-17	05-Jul-17												IEC/WB - Backfill up to Formation und
	A5740	IEC/WB - Subbase Laying 2 days	2d	06-Jul-17	07-Jul-17												IEC/WB - Subbase Laying 2 days
	A5750	IEC/WB - Asphalt (Road Base, Base Course, Wearing Course) 5 days	5d	08-Jul-17	12-Jul-17												IEC/WB - Asphalt (Road
	A5760	IEC/WB - Road Marking/Traffic Sign 3 days	3d	13-Jul-17	15-Jul-17												IEC/WB - Road Ma
	A5840	IEC/WB - Implement TTM	1d	16-Jul-17	16-Jul-17												IEC/WB - Implem
Stage 2 - Tsing Fung Street			28d	17-Jul-17	13-Aug-17												
	A5850	Decking /Footing Removal - 2 weeks	14d	17-Jul-17	30-Jul-17												
	A5880	Light Weight Conc. Ramp Rem. 4 weeks	28d	17-Jul-17	13-Aug-17												
	A5890	Trench Excavation for Towngas - 4 weeks	28d	17-Jul-17	13-Aug-17												
Reinstatement Existing Slopping & Vertical Sea Wall			55d	17-Jun-17	10-Aug-17												
Major Reinstatement Works for Seawall Reinstatement			55d	17-Jun-17	10-Aug-17												
Stage 1 - Removal of Remaining Pipe Pile Wall, Sheet Pile Wall & D-wall			55d	17-Jun-17	10-Aug-17												
	A7030	Backfill upto +2.5mPD at all bay of SR8	1d	17-Jun-17	17-Jun-17												Backfill upto +2.5mPD at all bay of SR8
	A7040	Cut pipe pile wall at A1 - A14	14d	18-Jun-17	01-Jul-17												Cut pipe pile wall at A1 - A14
	A7050	Under water cut sheet pile wall (36 nos.)	40d	02-Jul-17	10-Aug-17												
Works in Victoria Park (KD4, KD5, KD9)			184d	20-Jan-17 A	06-Sep-17												
Re-Provisioning Works			184d	20-Jan-17 A	06-Sep-17												
Nursery Compound			184d	20-Jan-17 A	06-Sep-17												
Submission			124d	20-Jan-17 A	27-Jun-17												
ABWF Submission			99d	01-Feb-17 A	02-Jun-17												
Material			99d	01-Feb-17 A	12-May-17												
	VP_NC_1060	ABWF Issue P.O. / Manufacturing / Fabrication	14d	01-Feb-17 A	18-Apr-17 A												ABWF Issue P.O. / Manufacturing / Fabrication
	VP_NC_1070	ABWF Materail Delivery	21d	19-Apr-17 A	12-May-17												ABWF Materail Delivery
Shop Drawing			14d	03-Feb-17 A	02-Jun-17												
	VP_NC_1090	ABWF Shop Drawing - ER Review and Approval	14d	03-Feb-17 A	02-Jun-17												ABWF Shop Drawing - ER Review and Approval
E&M Submission			124d	20-Jan-17 A	27-Jun-17												
Material			124d	20-Jan-17 A	27-Jun-17												



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Page 7 of 8

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip
Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
20-Apr-17	DWP-07 (6) - 3 Months Rolling	FS	TL

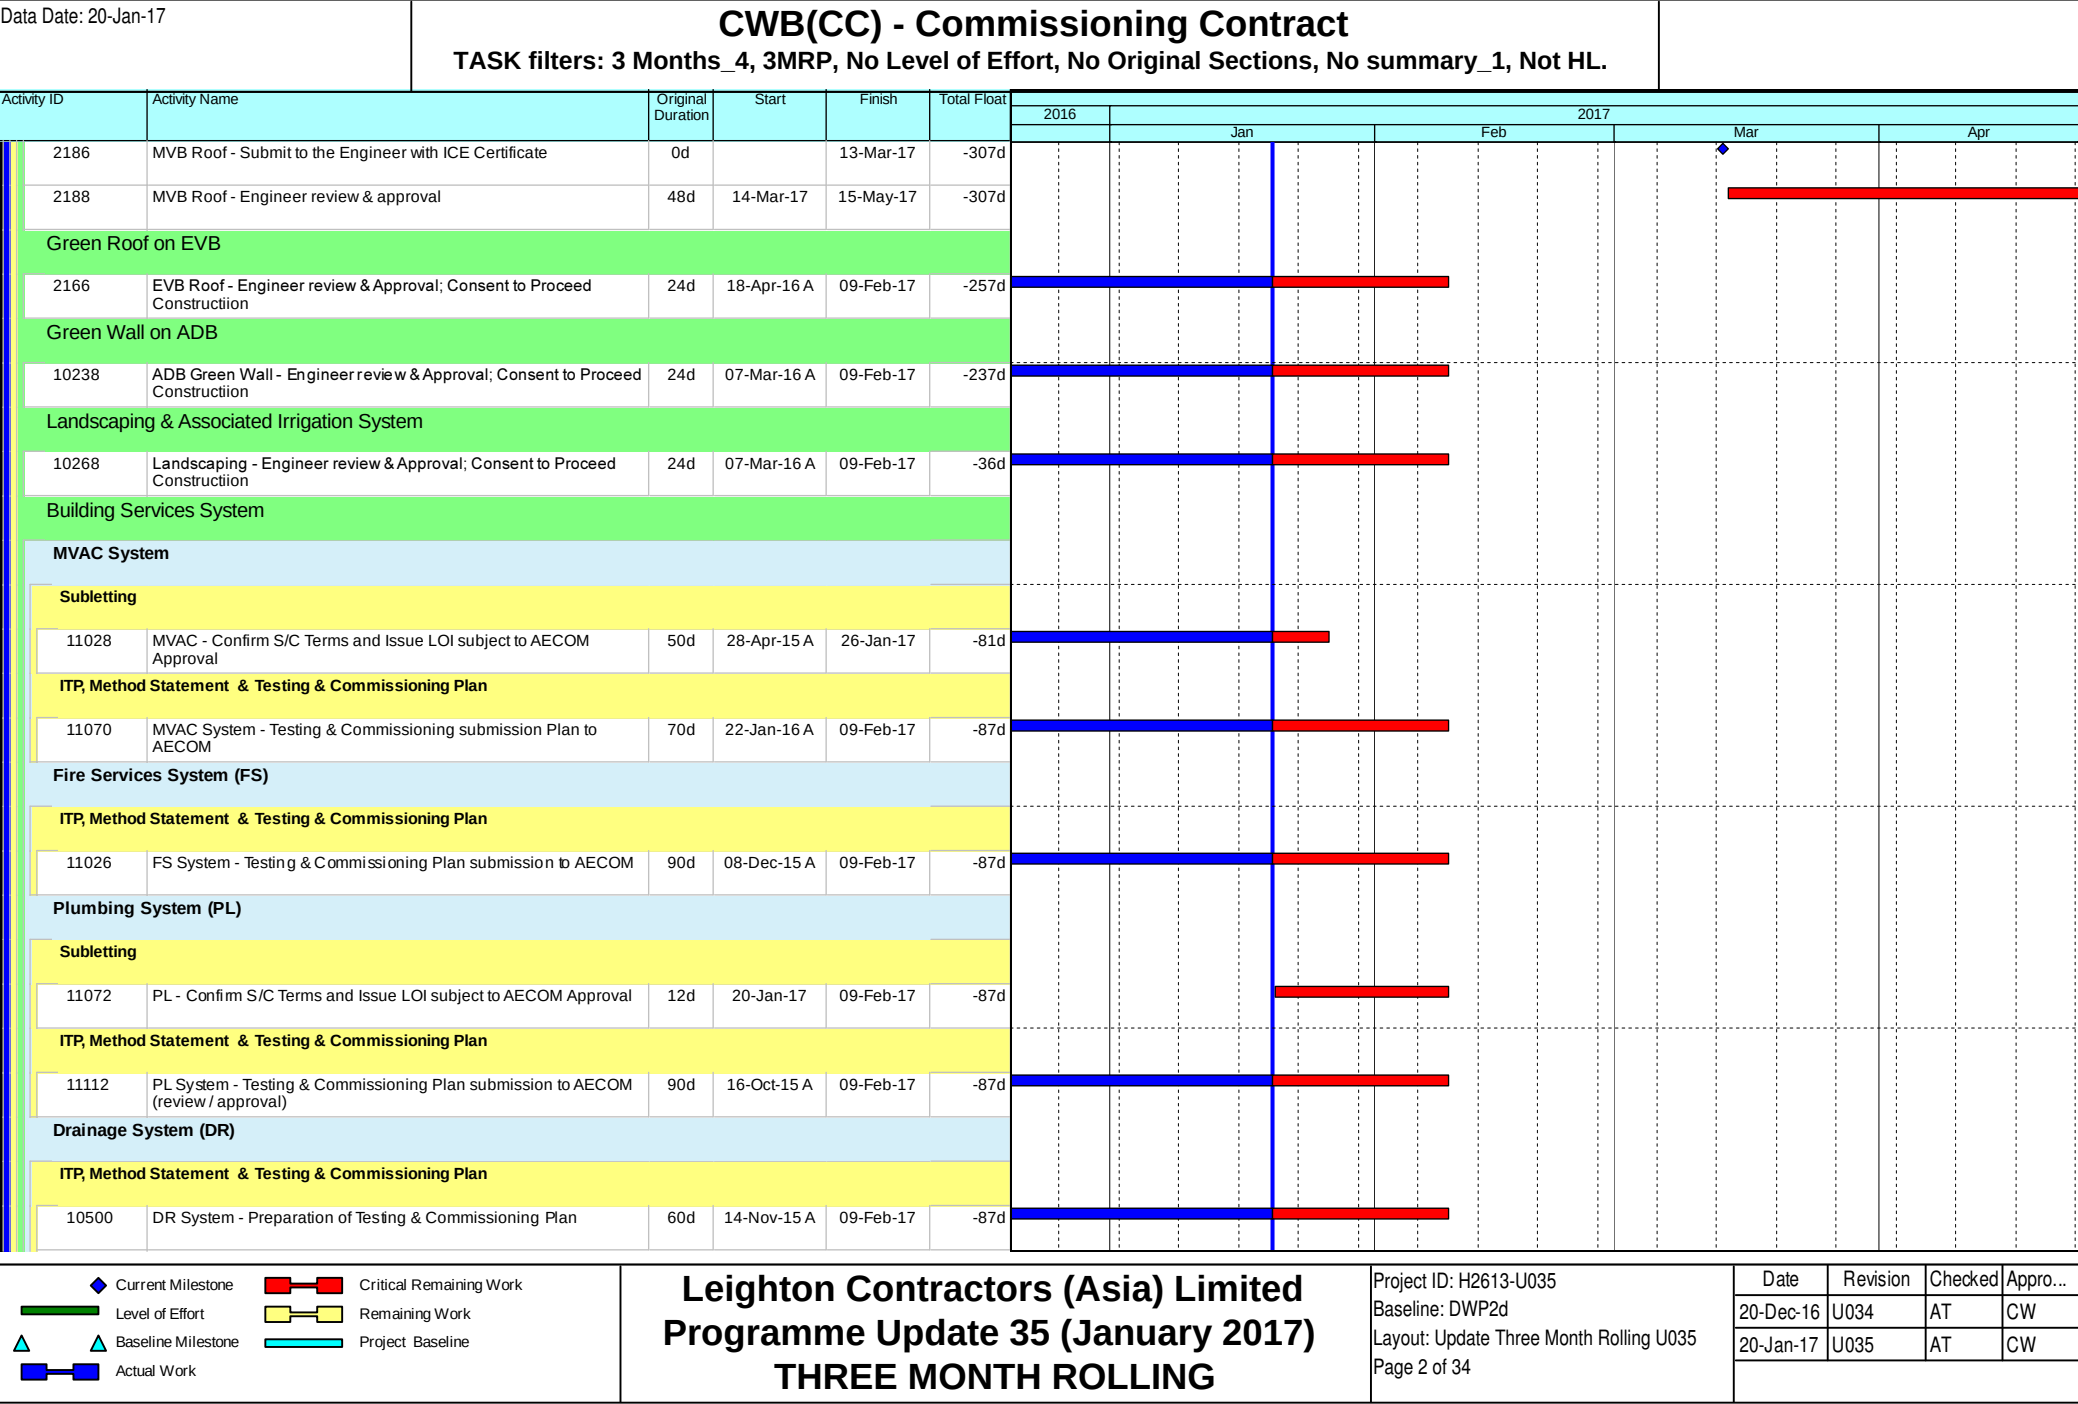
Activity ID	Activity Name	Original Duration	Start	Finish	2017											
					Apr			May			Jun			Jul		
VP_NC_1140	E&M Issue P.O. / Manufacturing / Fabrication	15d	20-Jan-17 A	22-May-17												
VP_NC_1150	E&M Materail Delivery	30d	23-May-17	27-Jun-17												
Shop Drawing		30d	20-Apr-17	26-May-17												
VP_NC_1170	E&M Shop Drawing - ER Review and Approval	30d	20-Apr-17	26-May-17												
Nursery compound		125d	09-Mar-17 A	06-Sep-17												
A4410	Concreting of two concrete plinths, 150 thick curbs and 1450H parapet wall above roof slab	7d	09-Mar-17 A	30-Mar-17 A												
A4420	ABWF, Plumbing Works, waterproofing and E&M works	60d	05-Apr-17 A	06-Sep-17												
KD11, KD12, KD13, KD18 Establishment Works for Landscape Softworks		1087d	23-Feb-15 A	09-Feb-18												
KD11 - Section 7A: Portion XIV & XV (Victoria Park Open Space)		885d	23-Feb-15 A	09-Feb-18												
EW_1000	Establishment Works - for Landscape Softworks and transplanted trees in Portion XIV & XV	901d	23-Feb-15 A	09-Feb-18												
KD12 - Section 7B: Portion VI & VII (Reprov. Bowling Green Area)		177d	03-Dec-15 A	20-Apr-17												
EW_1010	Establishment Works - for Landscape Softworks and transplanted trees in Portion VI & VII	177d	03-Dec-15 A	20-Apr-17												
KD10 - Preservation and Protection of Trees		1088d	21-Mar-13 A	20-Apr-17												
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	20-Apr-17												
KD15 & KD8 - Mooring Components Upkeep (CBTS and ATS)		980d	15-May-14 A	20-Apr-17												
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	20-Apr-17												
Works for Public Works Regional Laboratory (North Lantau) - KD1,KD16,KD17)		1301d	19-Jul-13 A	21-Nov-17												
KD17 - Maintenance and Upkeep of New PWRL (Portion XVII)		1301d	19-Jul-13 A	21-Nov-17												
PWRL_1050	Maintenance/ Upkeep of New PWRL	1301d	19-Jul-13 A	21-Nov-17												

China State Construction Engineering (Hong Kong) Ltd.

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

Activity Name	Start	Finish	2017		
			Apr	May	Jun
Hung Hing Road Resurfacing	1/6/2017	30/6/2017			
Defect works inside tunnel	1/4/2017	30/9/2017			

Data Date: 20-Jan-17						CWB(CC) - Commissioning Contract																									
						TASK filters: 3 Months_4, 3MRP, No Level of Effort, No Original Sections, No summary_1, Not HL.																									
Activity ID		Activity Name				Original Duration	Start	Finish	Total Float																						
										2016	2017																				
											Jan			Feb			Mar			Apr											
Update 2017-01-20 CWB(CC) - Commissioning Contract (DWP R2d)																															
PRELIMINARIES AND GENERAL REQUIREMENTS																															
Salient Key Dates and Milestones																															
Contract Key Dates																															
KD001	KD1 - Achievement of Stage 1 (1054 days)					0d		16-Jan-17 A																							
Possession Dates and Vacation Dates																															
PO-IVb	Possession of Portion IVb (Day 930) - MVB (Split into 2 sections)					261d	20-Dec-16 A	20-Dec-16 A																							
PO-VIb_a	Possession of Portion VIb (Day 761) - CH3400-3428					303d	20-Jan-17	18-Nov-17	-284d																						
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3					303d	20-Jan-17	18-Nov-17	-315d																						
PO-IVa2	Possession of Portion IVa (Day 930) - CH2720-2950 / SR1					260d	01-Feb-17	18-Oct-17	-193d																						
PO-VIIIa	Possession of Portion VIIIa (Day 929) - CH4250-4600					246d	15-Feb-17	18-Oct-17	-348d																						
PO-VIIIb	Possession of Portion VIIIb (Day 929) - SR8 (CH700-350)					233d	28-Feb-17	18-Oct-17	-397d																						
PO-VIIIc	Possession of Portion IIIlc (Day 1039) - SR8 (CH350-310) / SCP4					233d	28-Feb-17	18-Oct-17	-124d																						
PO-IVb2	Possession of Portion IVb (Day 930) - MVB (GL D-H)					233d	28-Feb-17	18-Oct-17	-365d																						
PO-IVb1	Possession of Portion IVb (Day 930) - MVB (GL A-D)					261d	31-Mar-17	16-Dec-17	-338d																						
Submissions and Approvals																															
Initial General Submission																															
1211	Submission of 1st Project video film					0d		20-Jan-17*	-354d																						
9932	Submission of 1st Project video film Video1 / Video2 (Release II)					0d		20-Jan-17*	-719d																						
DETAILED DESIGN OF WORKS																															
Permanent Works Design and Engineering																															
Metal Roof on MVB																															
2182	MVB Roof - Prepare Preliminary Design and Submission (Schematics)					48d	01-Dec-15 A	13-Feb-17	-307d																						
2182a	MVB Roof - Pending for RFI reply for Schematic design					24d	14-Jan-16 A	04-Jan-17 A																							
2184	MVB Roof - Finalise preliminary design and ICE Review					24d	14-Feb-17	13-Mar-17	-307d																						
◆ Current Milestone ▬ Level of Effort ▲ Baseline Milestone ■ Actual Work ▬ Critical Remaining Work ▬ Remaining Work ▬ Project Baseline						Leighton Contractors (Asia) Limited Programme Update 35 (January 2017) THREE MONTH ROLLING						Project ID: H2613-U035 Baseline: DWP2d Layout: Update Three Month Rolling U035 Page 1 of 34				<table><tr><td>Date</td><td>Revision</td><td>Checked</td><td>Appro...</td></tr><tr><td>20-Dec-16</td><td>U034</td><td>AT</td><td>CW</td></tr><tr><td>20-Jan-17</td><td>U035</td><td>AT</td><td>CW</td></tr></table>				Date	Revision	Checked	Appro...	20-Dec-16	U034	AT	CW	20-Jan-17	U035	AT	CW
Date	Revision	Checked	Appro...																												
20-Dec-16	U034	AT	CW																												
20-Jan-17	U035	AT	CW																												



Data Date: 20-Jan-17		CWB(CC) - Commissioning Contract TASK filters: 3 Months_4, 3MRP, No Level of Effort, No Original Sections, No summary_1, Not HL.														
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float											
						2016	2017									
							Jan		Feb		Mar		Apr			
Traffic Control and Surveillance System (TCSS)																
Procurement & Fabrication																
12478	TCSS - FAT for all plants, materials & equipments	197d	16-Dec-15 A	08-Feb-17	-348d											
Building Services System																
Shop Drawings / CSD / CBWD																
2306	BS(WVB) - Obtain Approval for Shop Drawings, CSD & CBWD	0d		20-Jan-17	195d											
2314	BS(MVB) - Obtain Approval for Shop Drawings, CSD & CBWD	0d		20-Jan-17	239d											
2318	BS(EVB) - Obtain Approval for Shop Drawings, CSD & CBWD	0d		20-Jan-17	195d											
Thermal Barriers																
Procurement & Fabrication																
12824	TB - Delivery for Thermal Barriers materials(remaining batches)	90d	27-Jun-15 A	18-Feb-17	-149d											
CONSTRUCTION																
West Ventilation Building (WVB - related)																
Tunnel Section (WVB-related)																
Portion Ia [CH840 to CH1360]																
4902	Ia - Initial Site Survey	6d	30-Jun-16 A	26-Jan-17	-216d											
13086a	Request for VO / instruction for TCSS equipment installation and cabling (Ganty FADS01) (Ref: H27613-LJV-ME-LE-4022)	24d	04-Oct-16 A	14-Mar-17	-167d											
13086	TCSS cabling and sign face installation (FADS01) - Start date is tentative and need to be confirmed at a later stage	40d	15-Mar-17	06-May-17	-167d											
Westbound																
4904	Ia(WB) - Mobilisation & Setup	6d	27-Jan-17	09-Feb-17	-216d											
5000	MEP(WB) - (CH840 to CH1360) E&M 1st Fix	29d	10-Feb-17	15-Mar-17	-216d											
5008	MEP(WB) - (CH840 to CH1360) E&M 2nd Fix (include Sump A)	58d	16-Mar-17	29-May-17	-216d											
Eastbound																
6110	Ia(EB) - Mobilisation & Setup	2d	27-Jan-17	04-Feb-17	-212d											
6100	MEP(EB) - (CH840 to CH1360) E&M 1st Fix	29d	06-Feb-17	10-Mar-17	-212d											

Current Milestone

Level of Effort

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 35 (January 2017)

THREE MONTH ROLLING

Project ID: H2613-U035

Baseline: DWP2d

Layout: Update Three Month Rolling U035

Page 5 of 34

Date

20-Dec-16

20-Jan-17

Revision

U034

U035

Checked

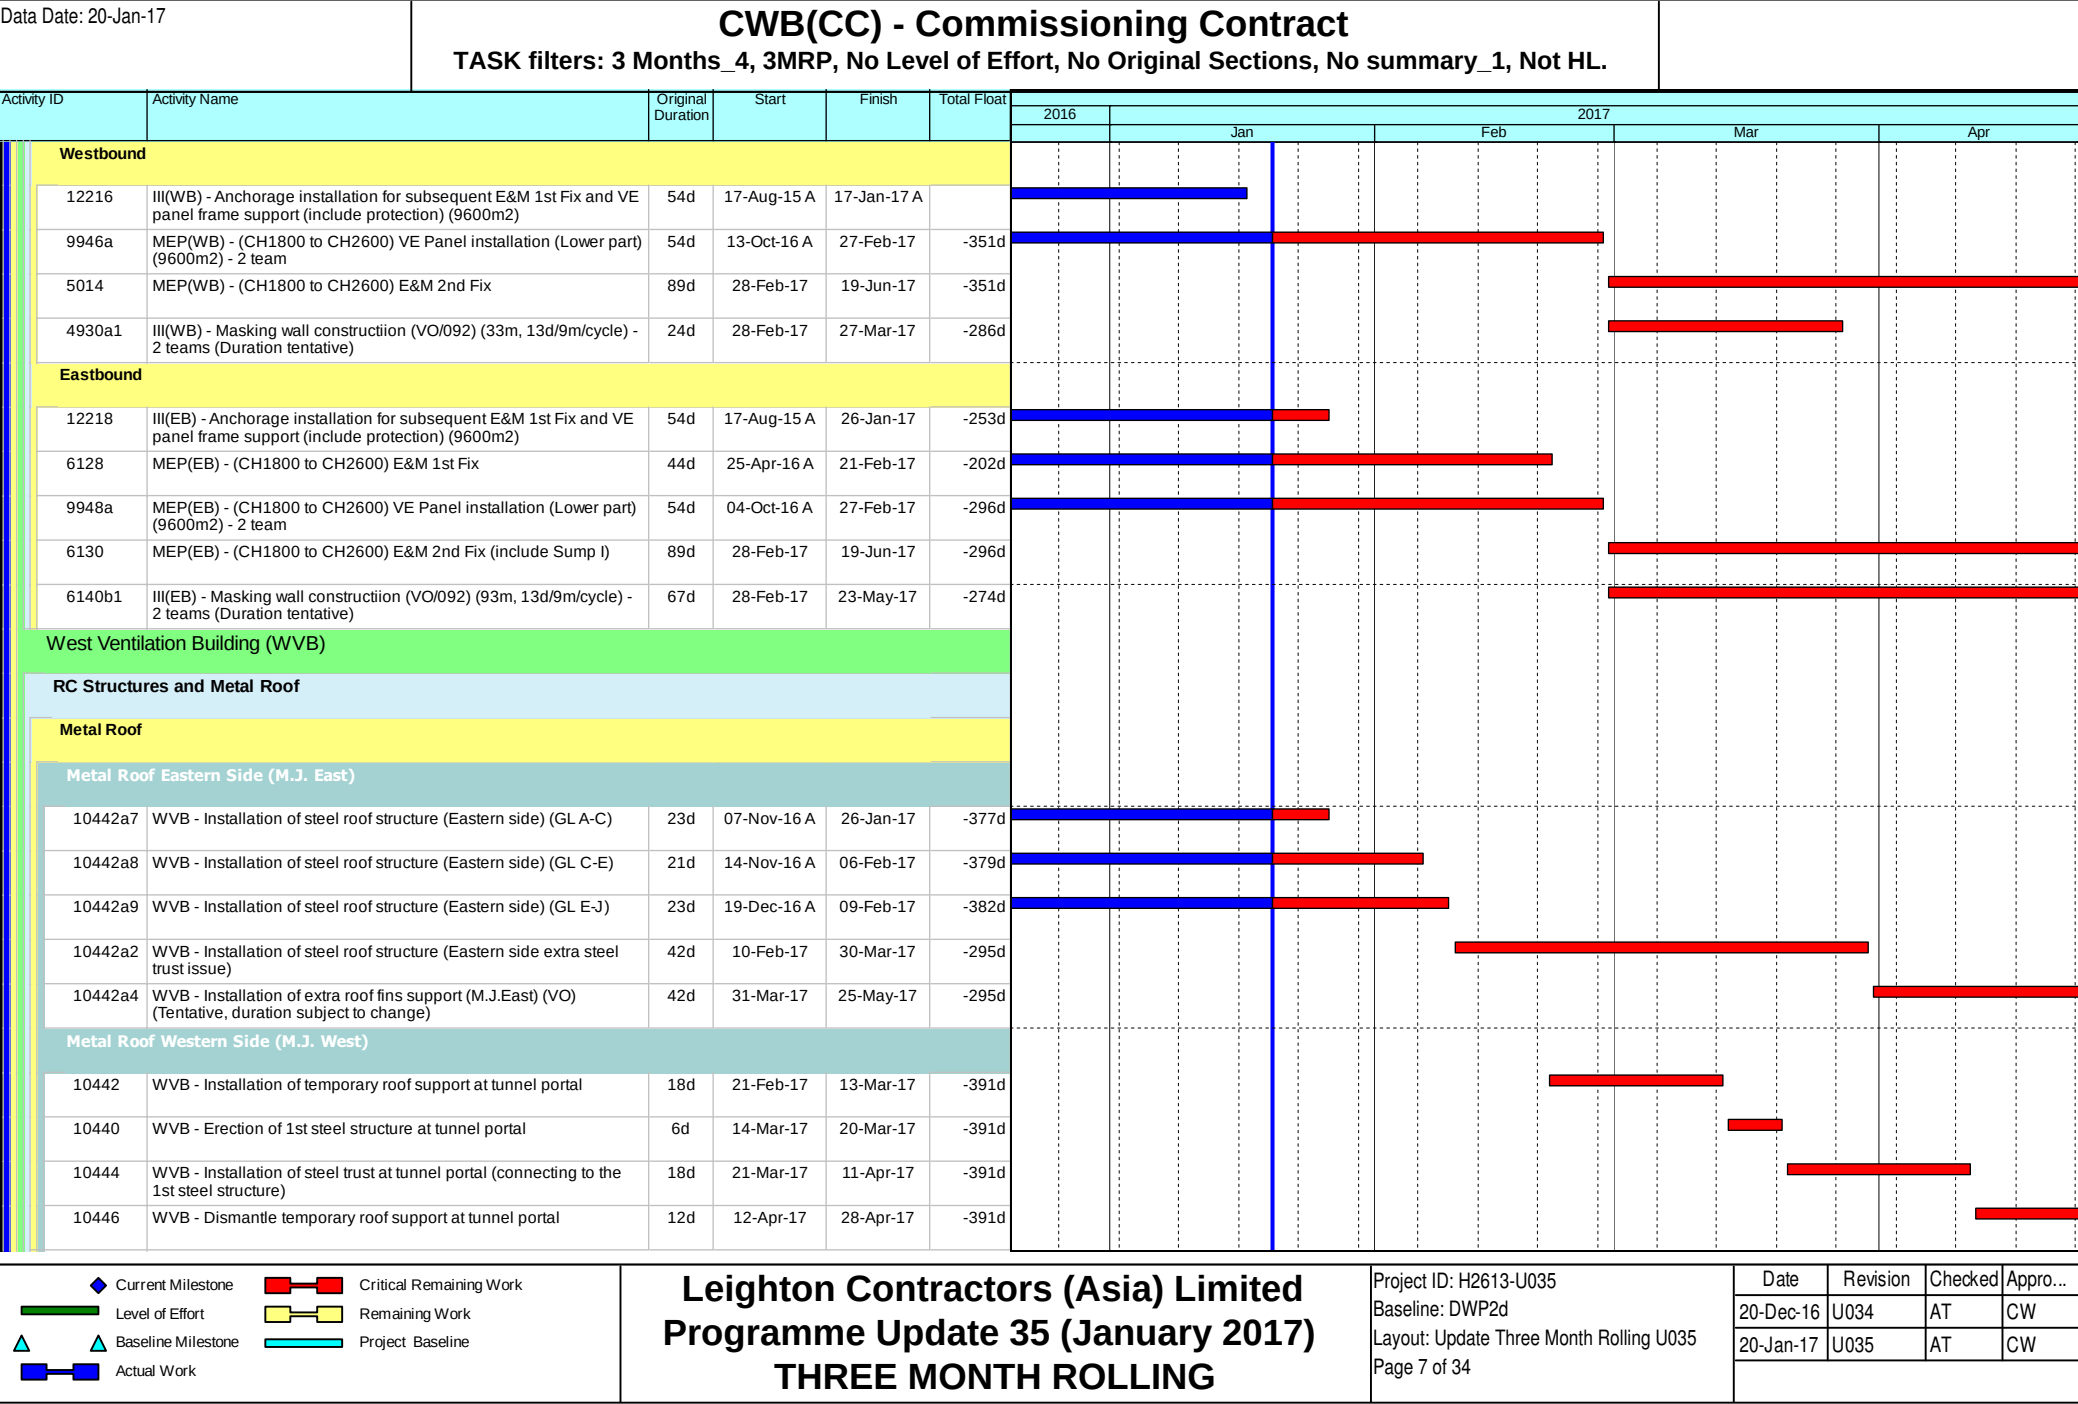
AT

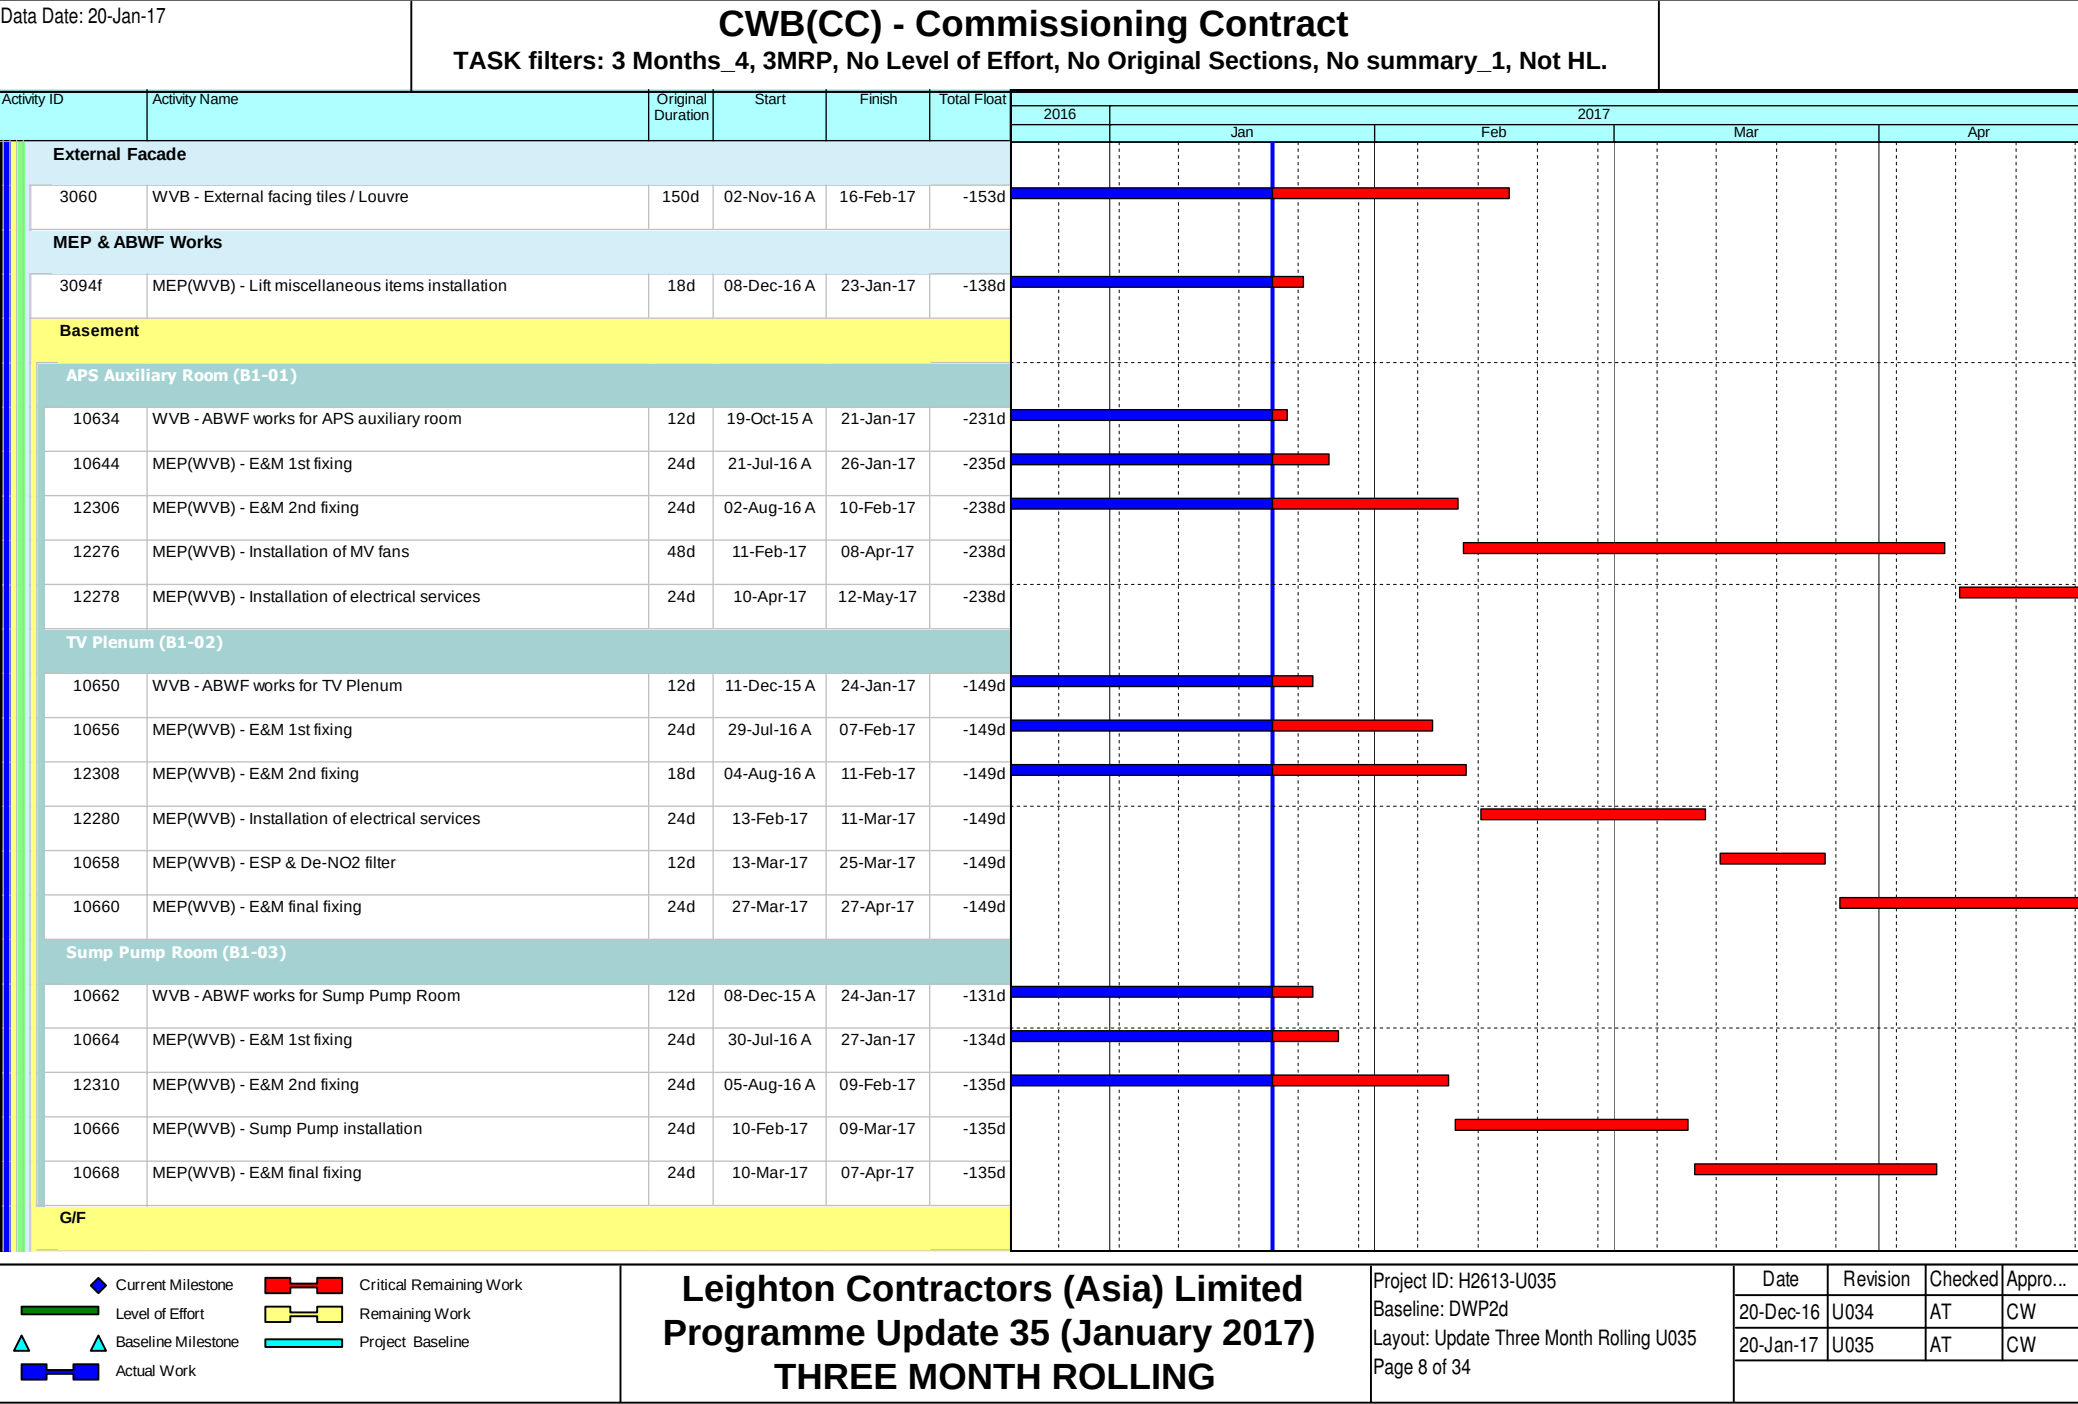
AT

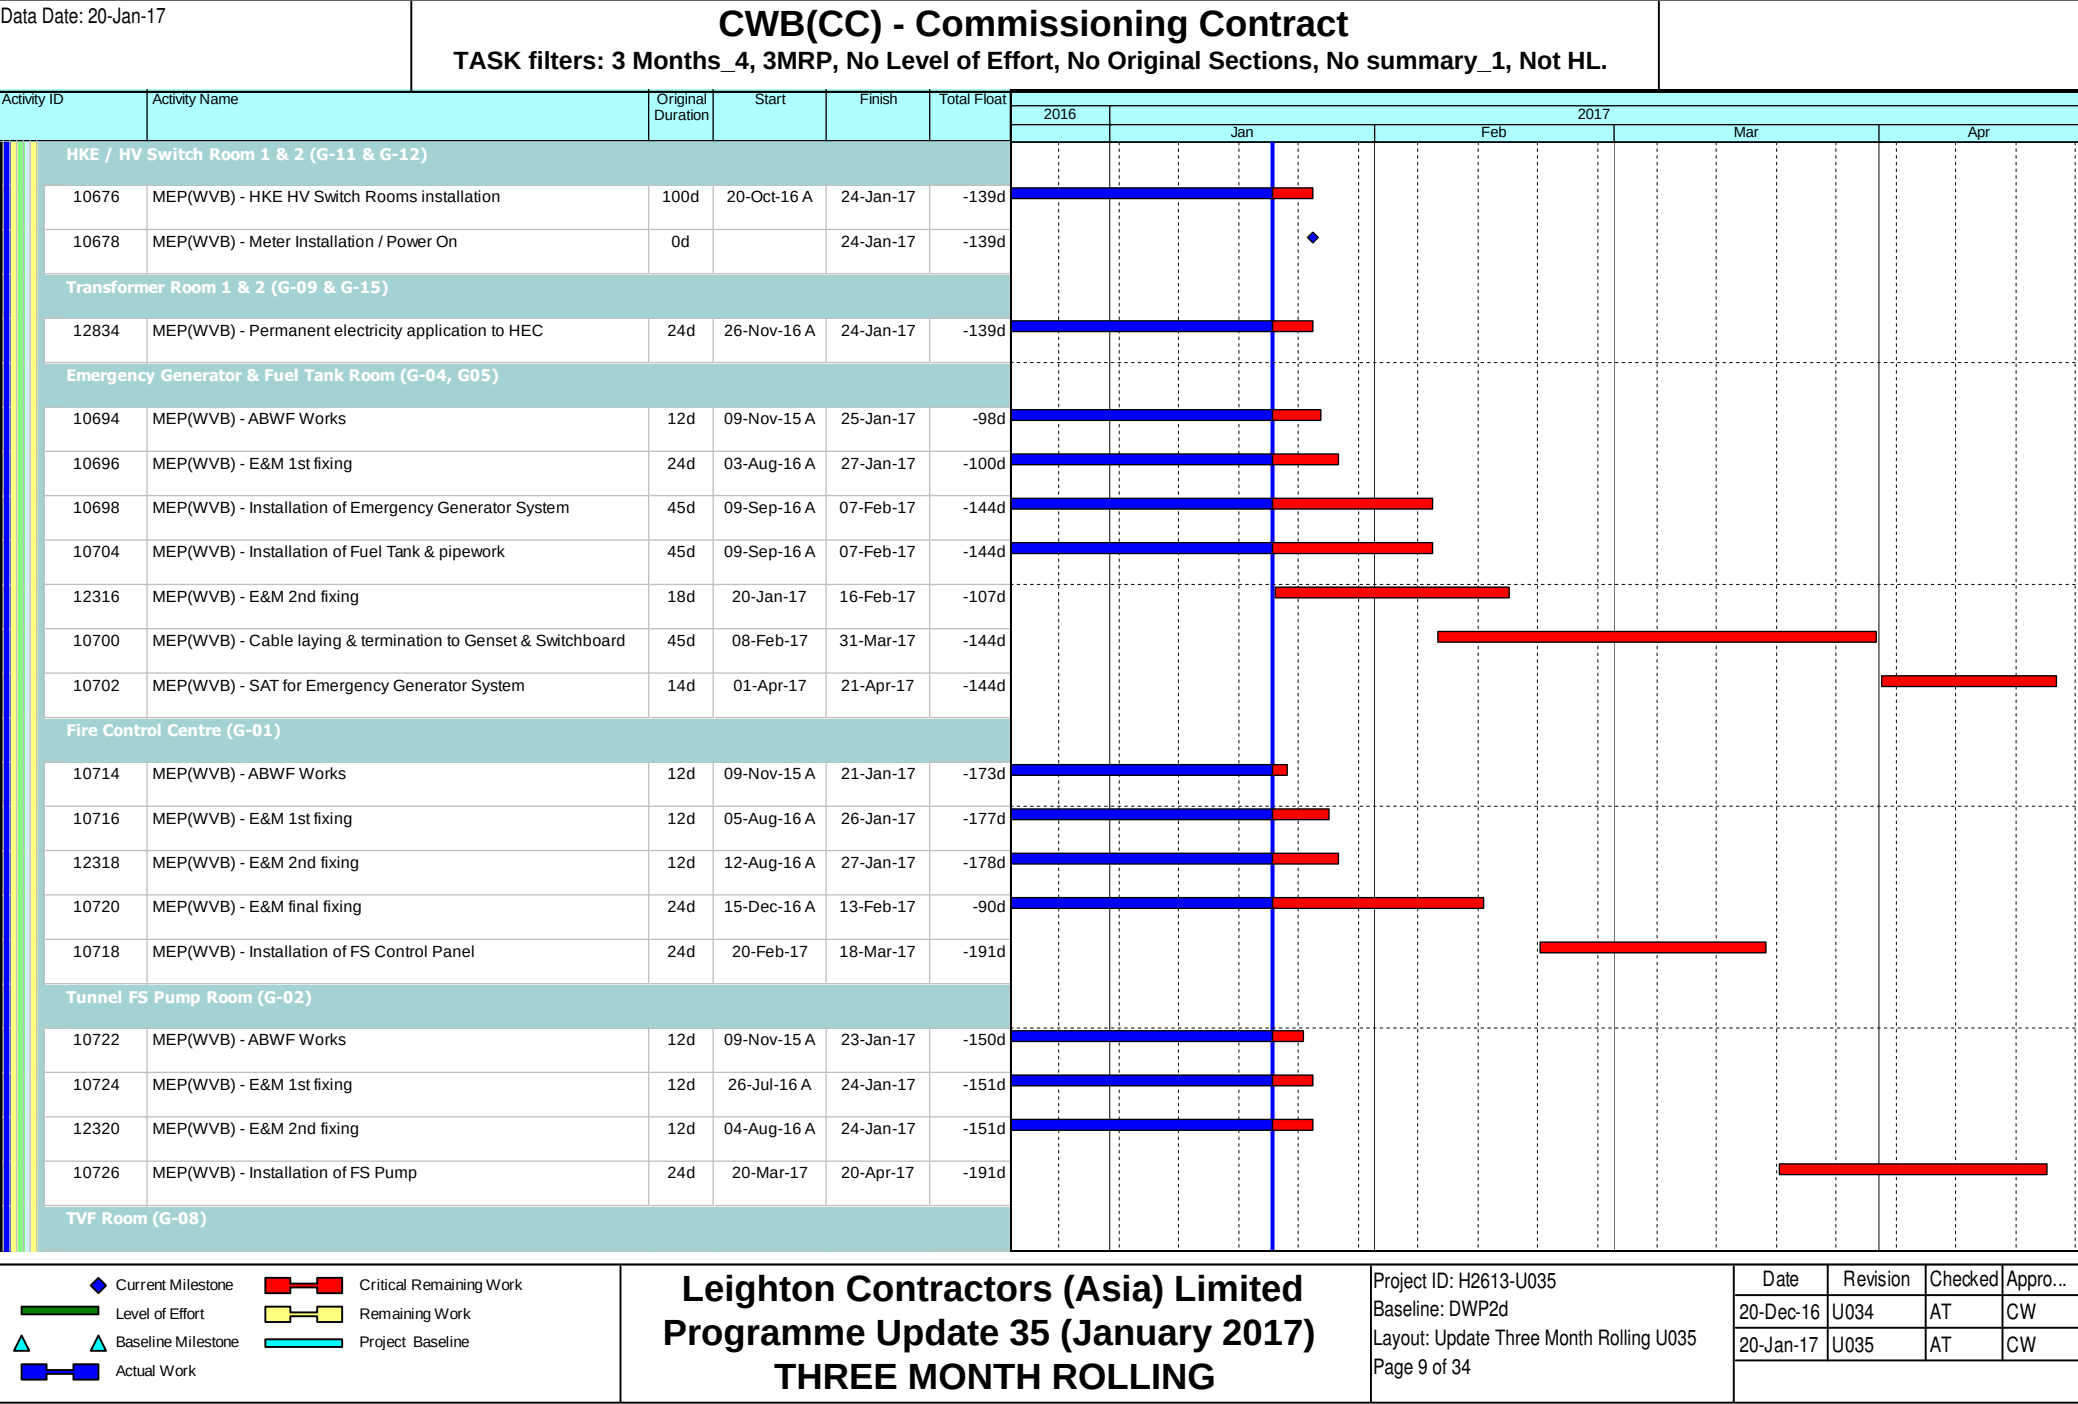
Appro...

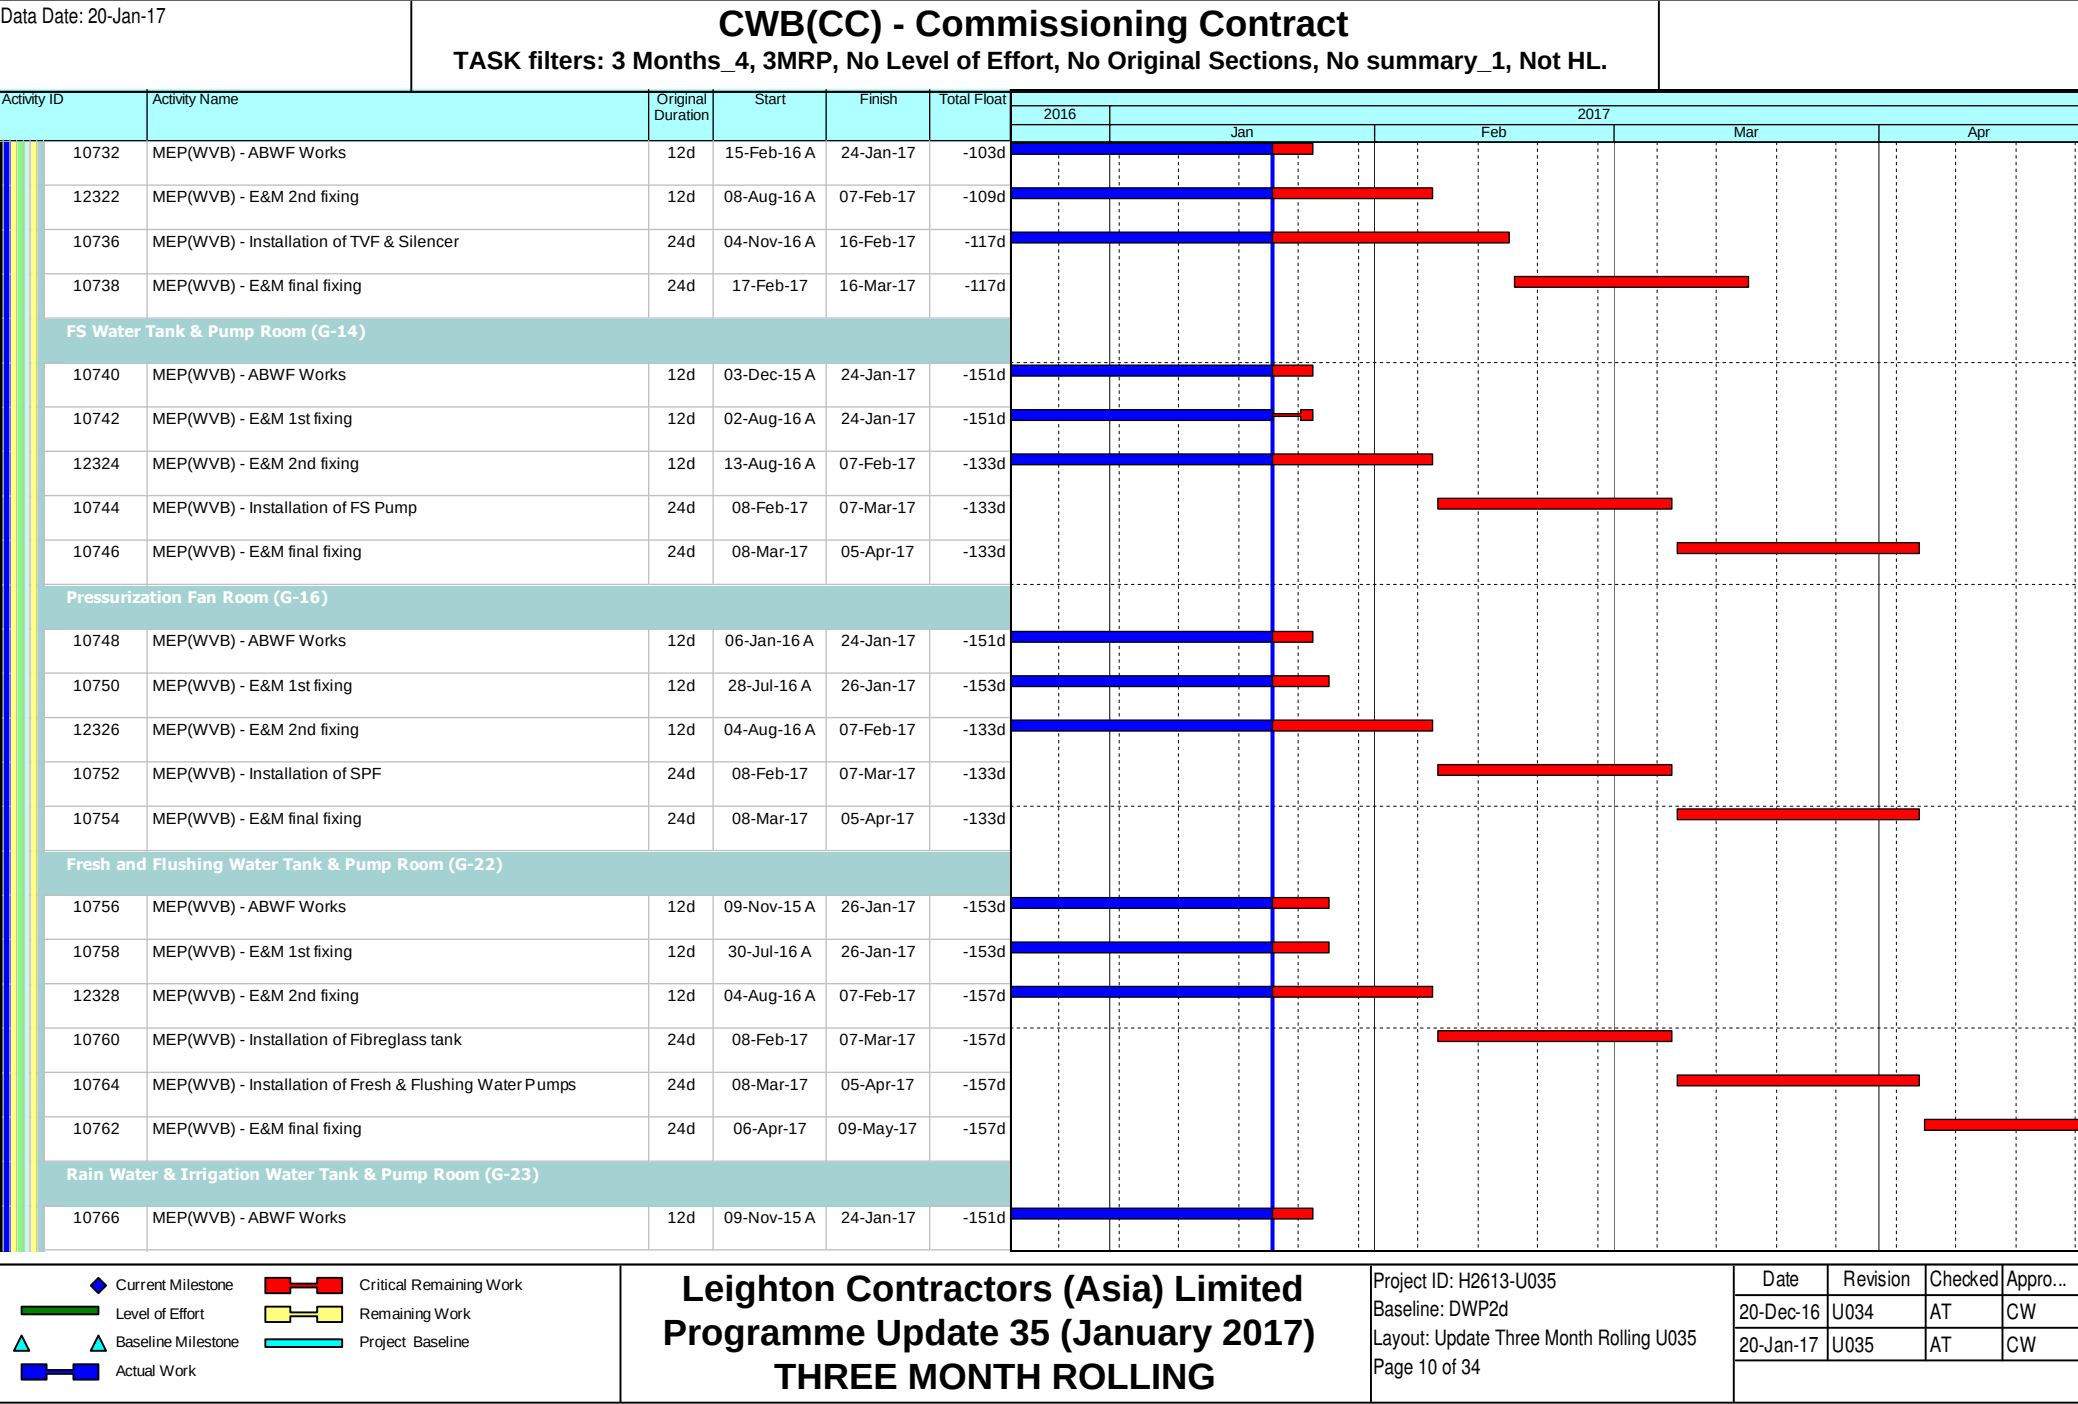
CW

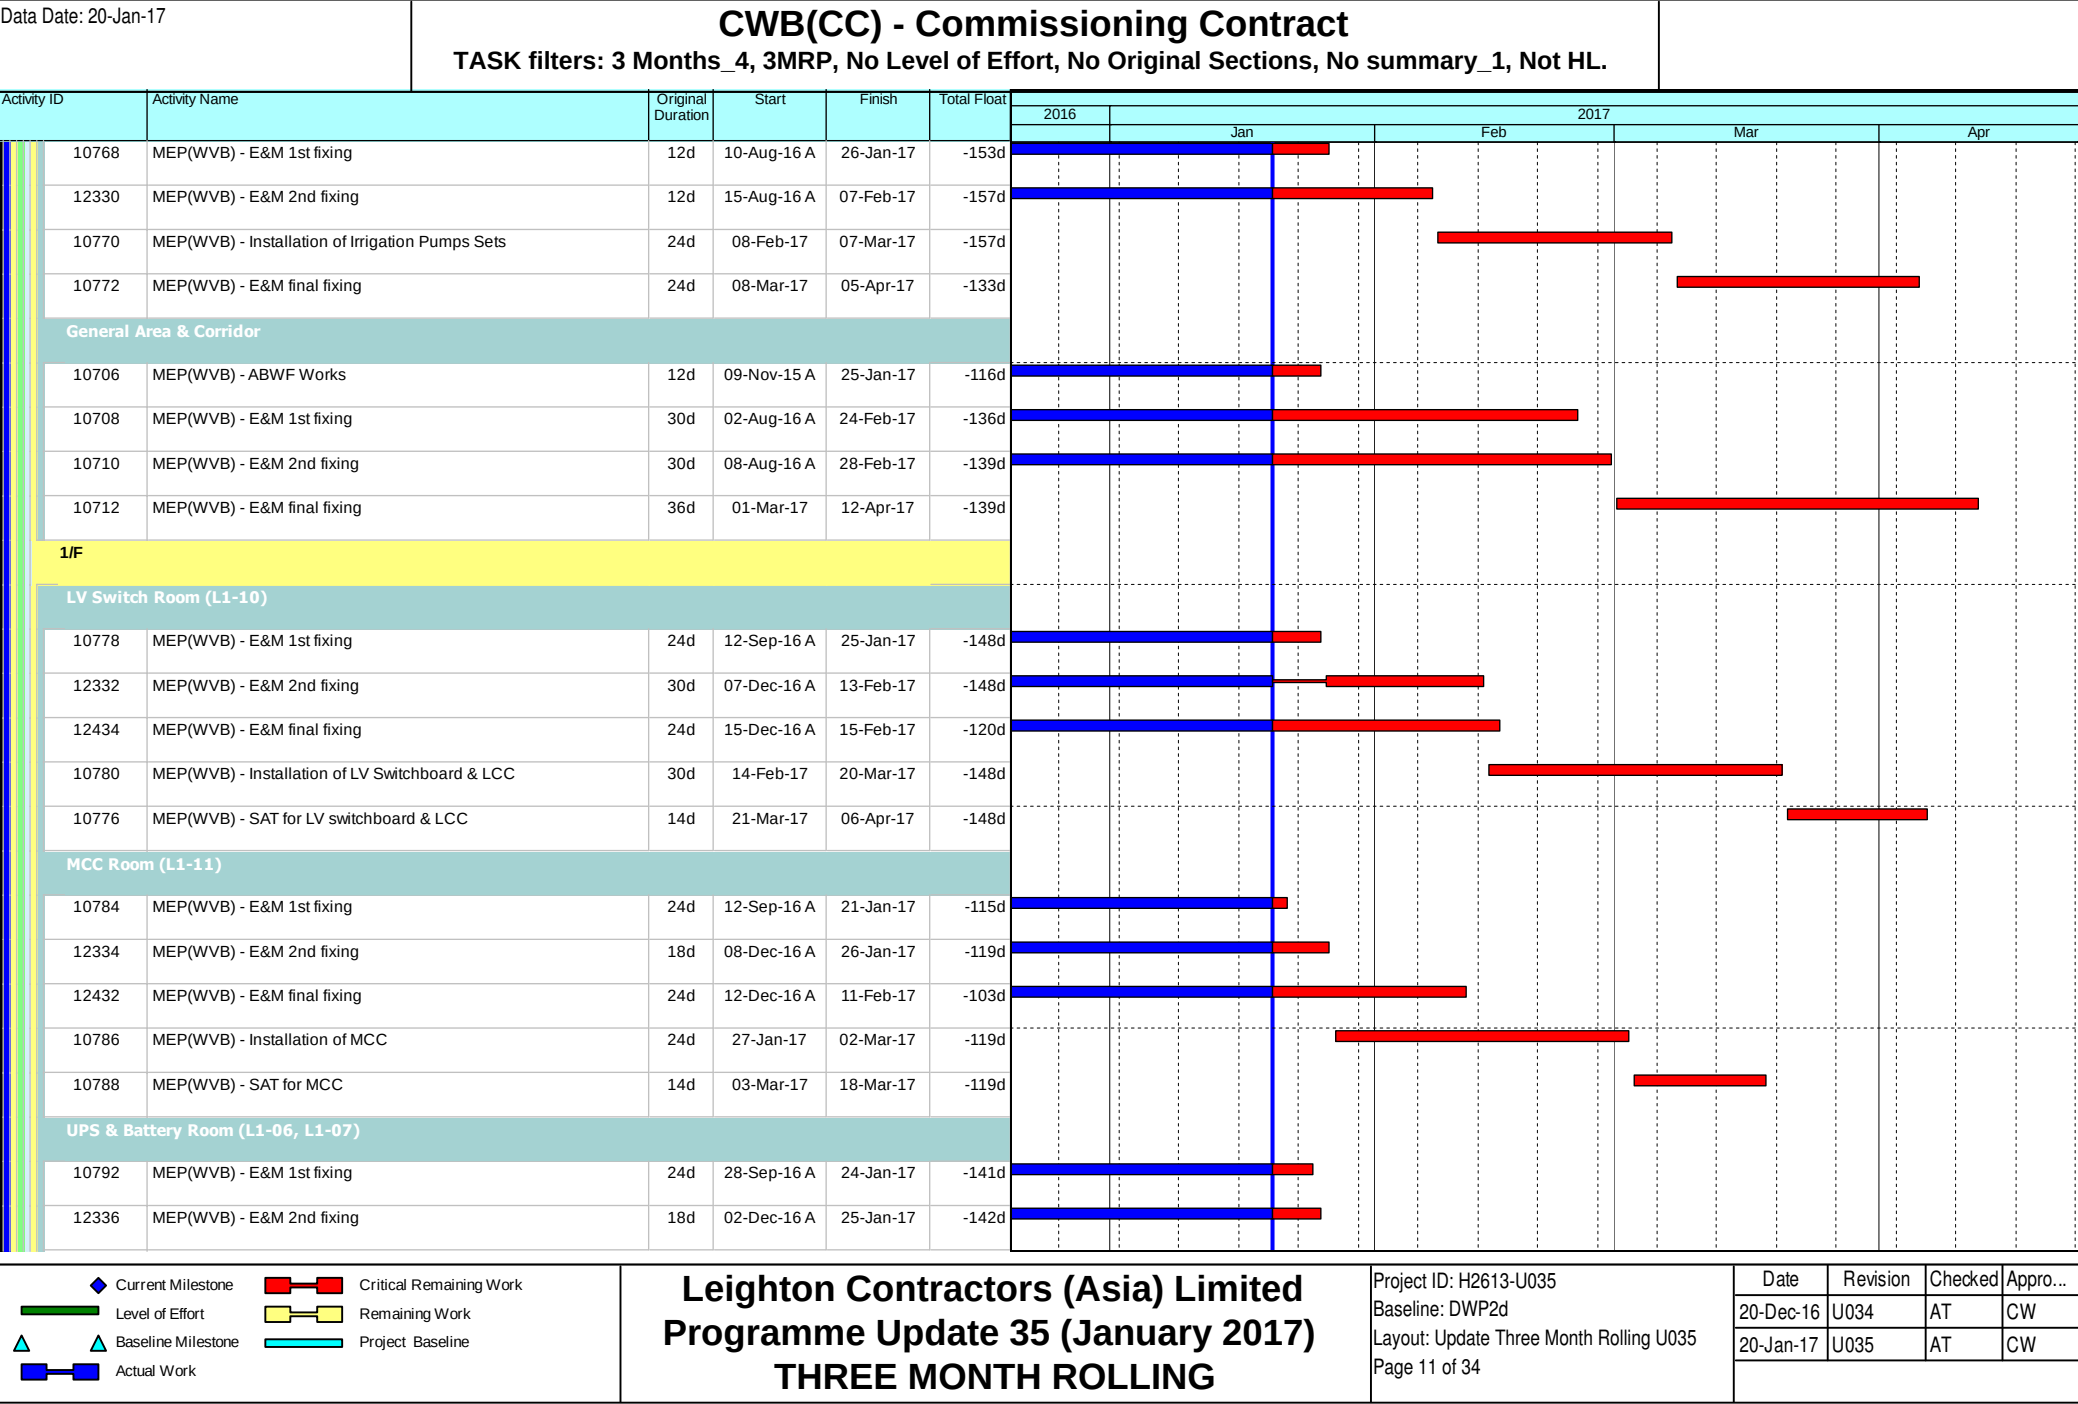
CW

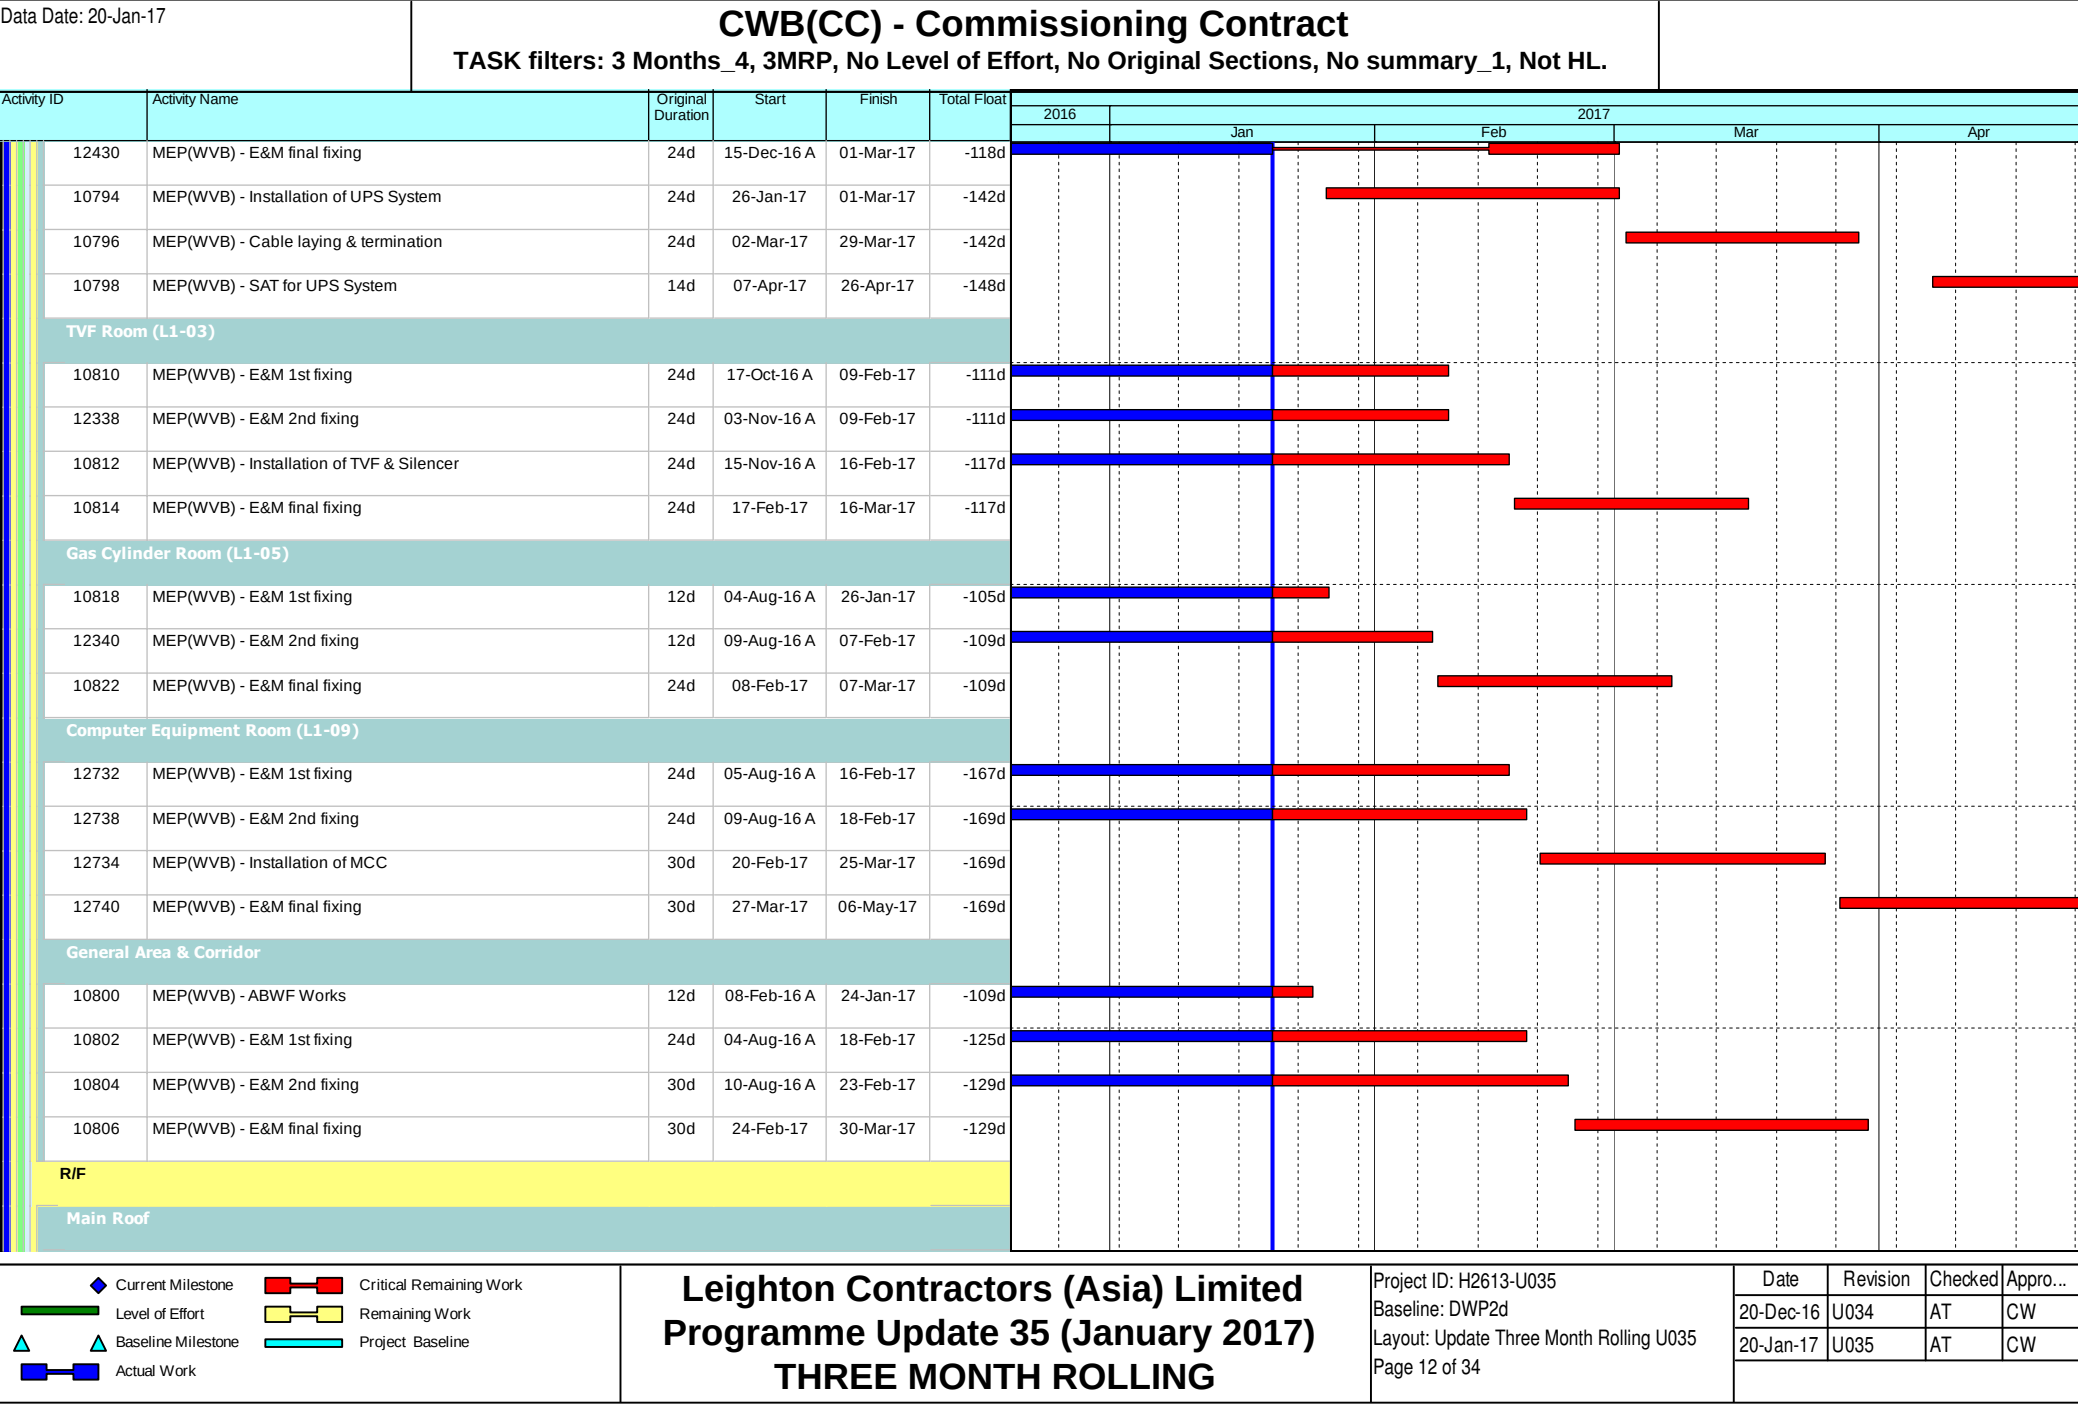


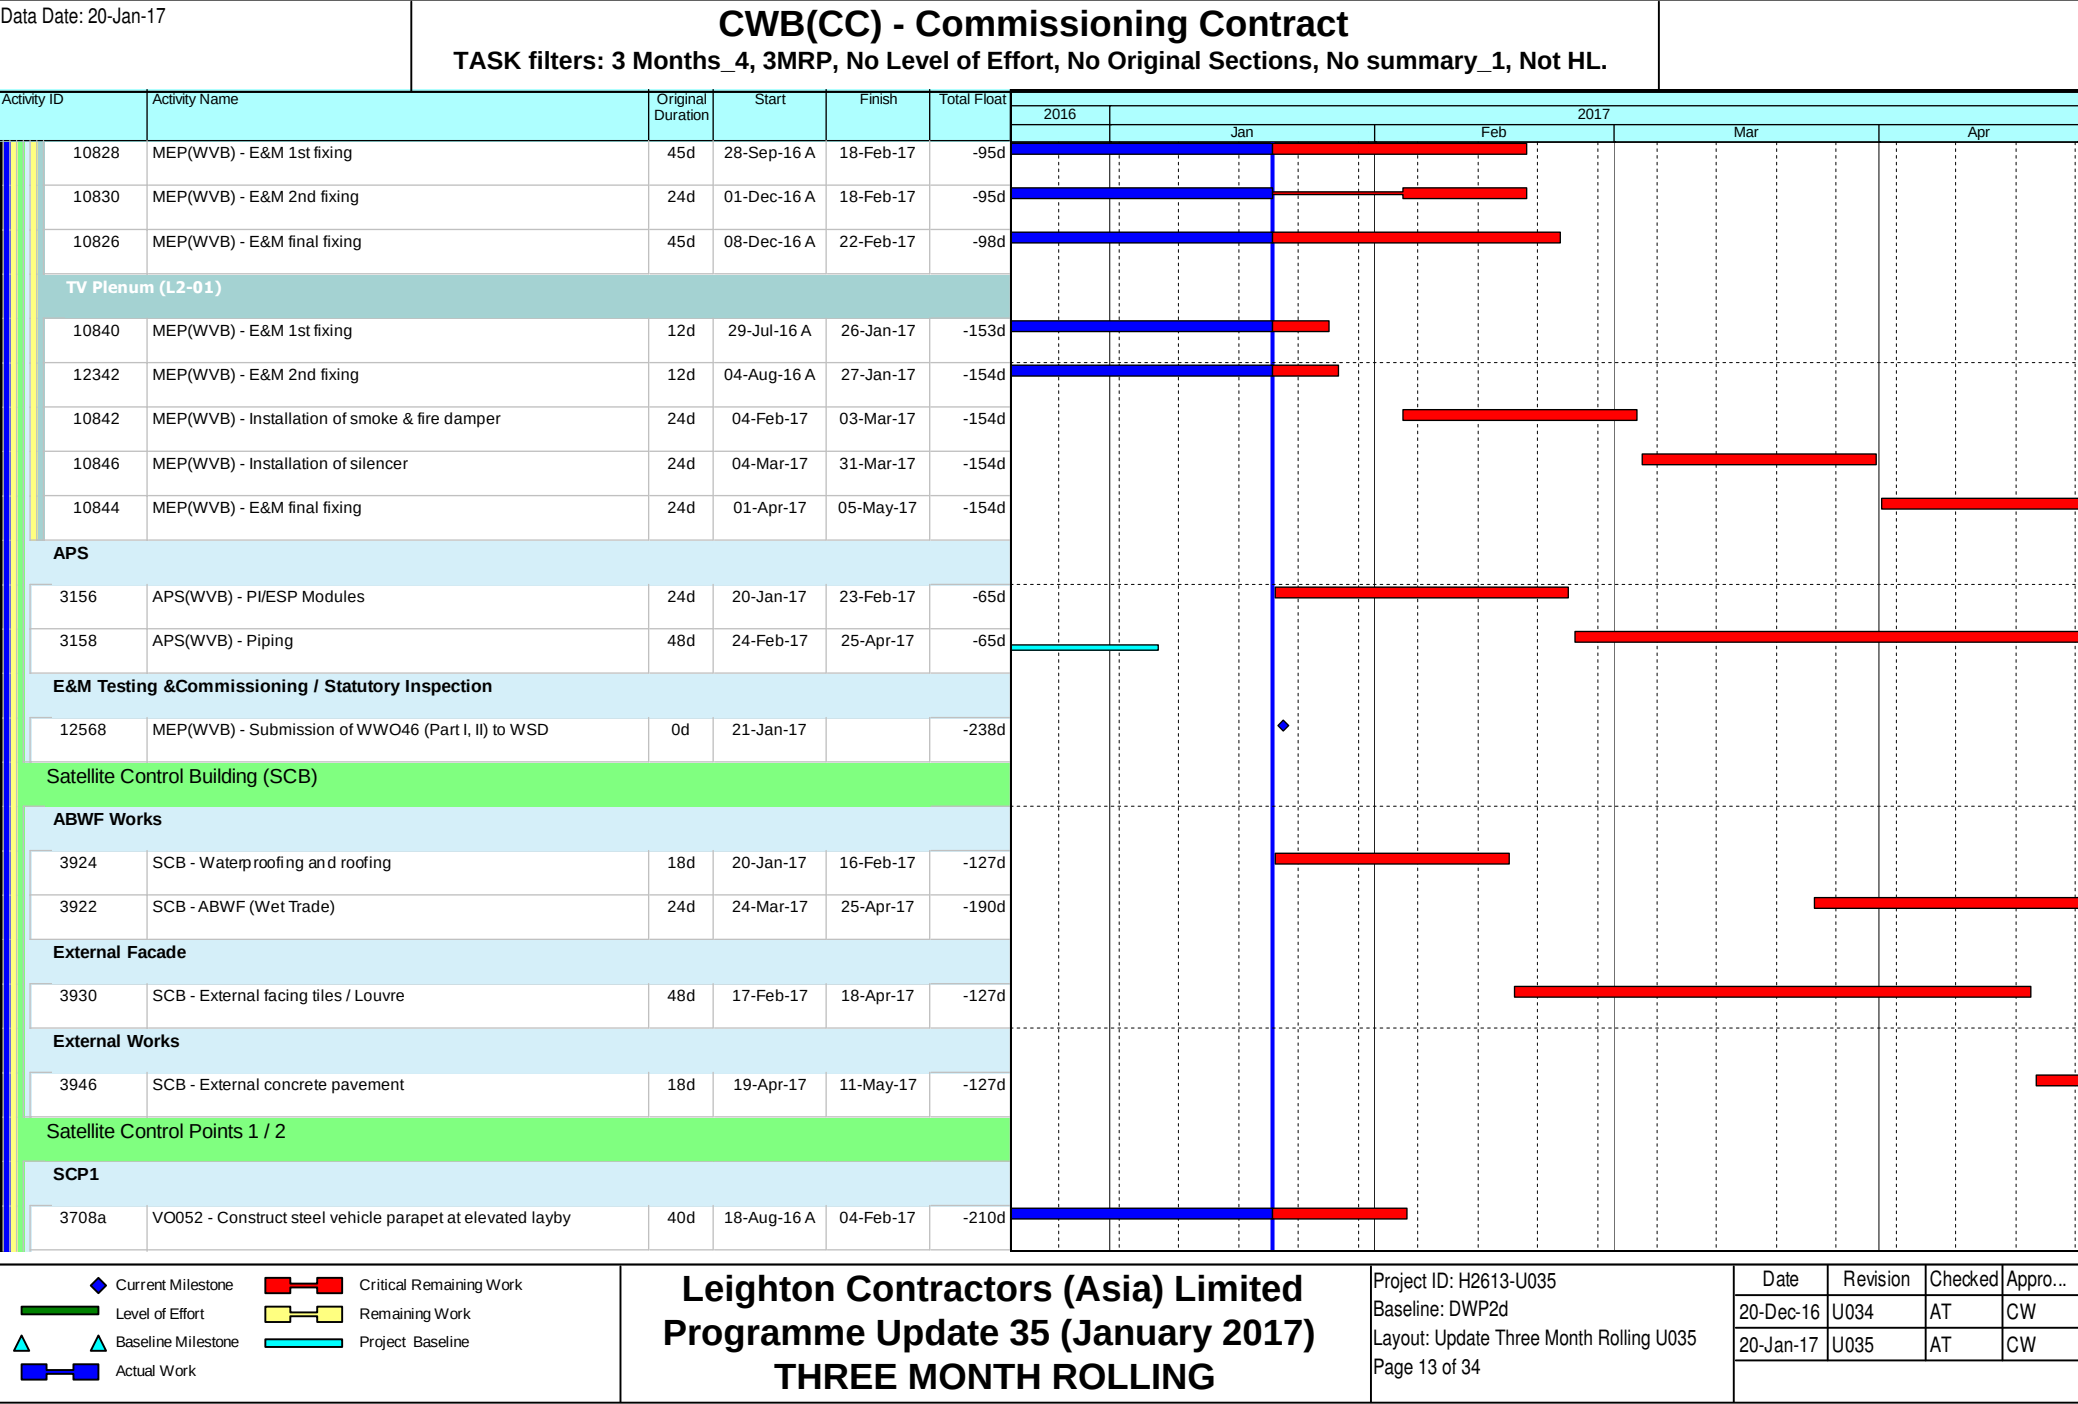


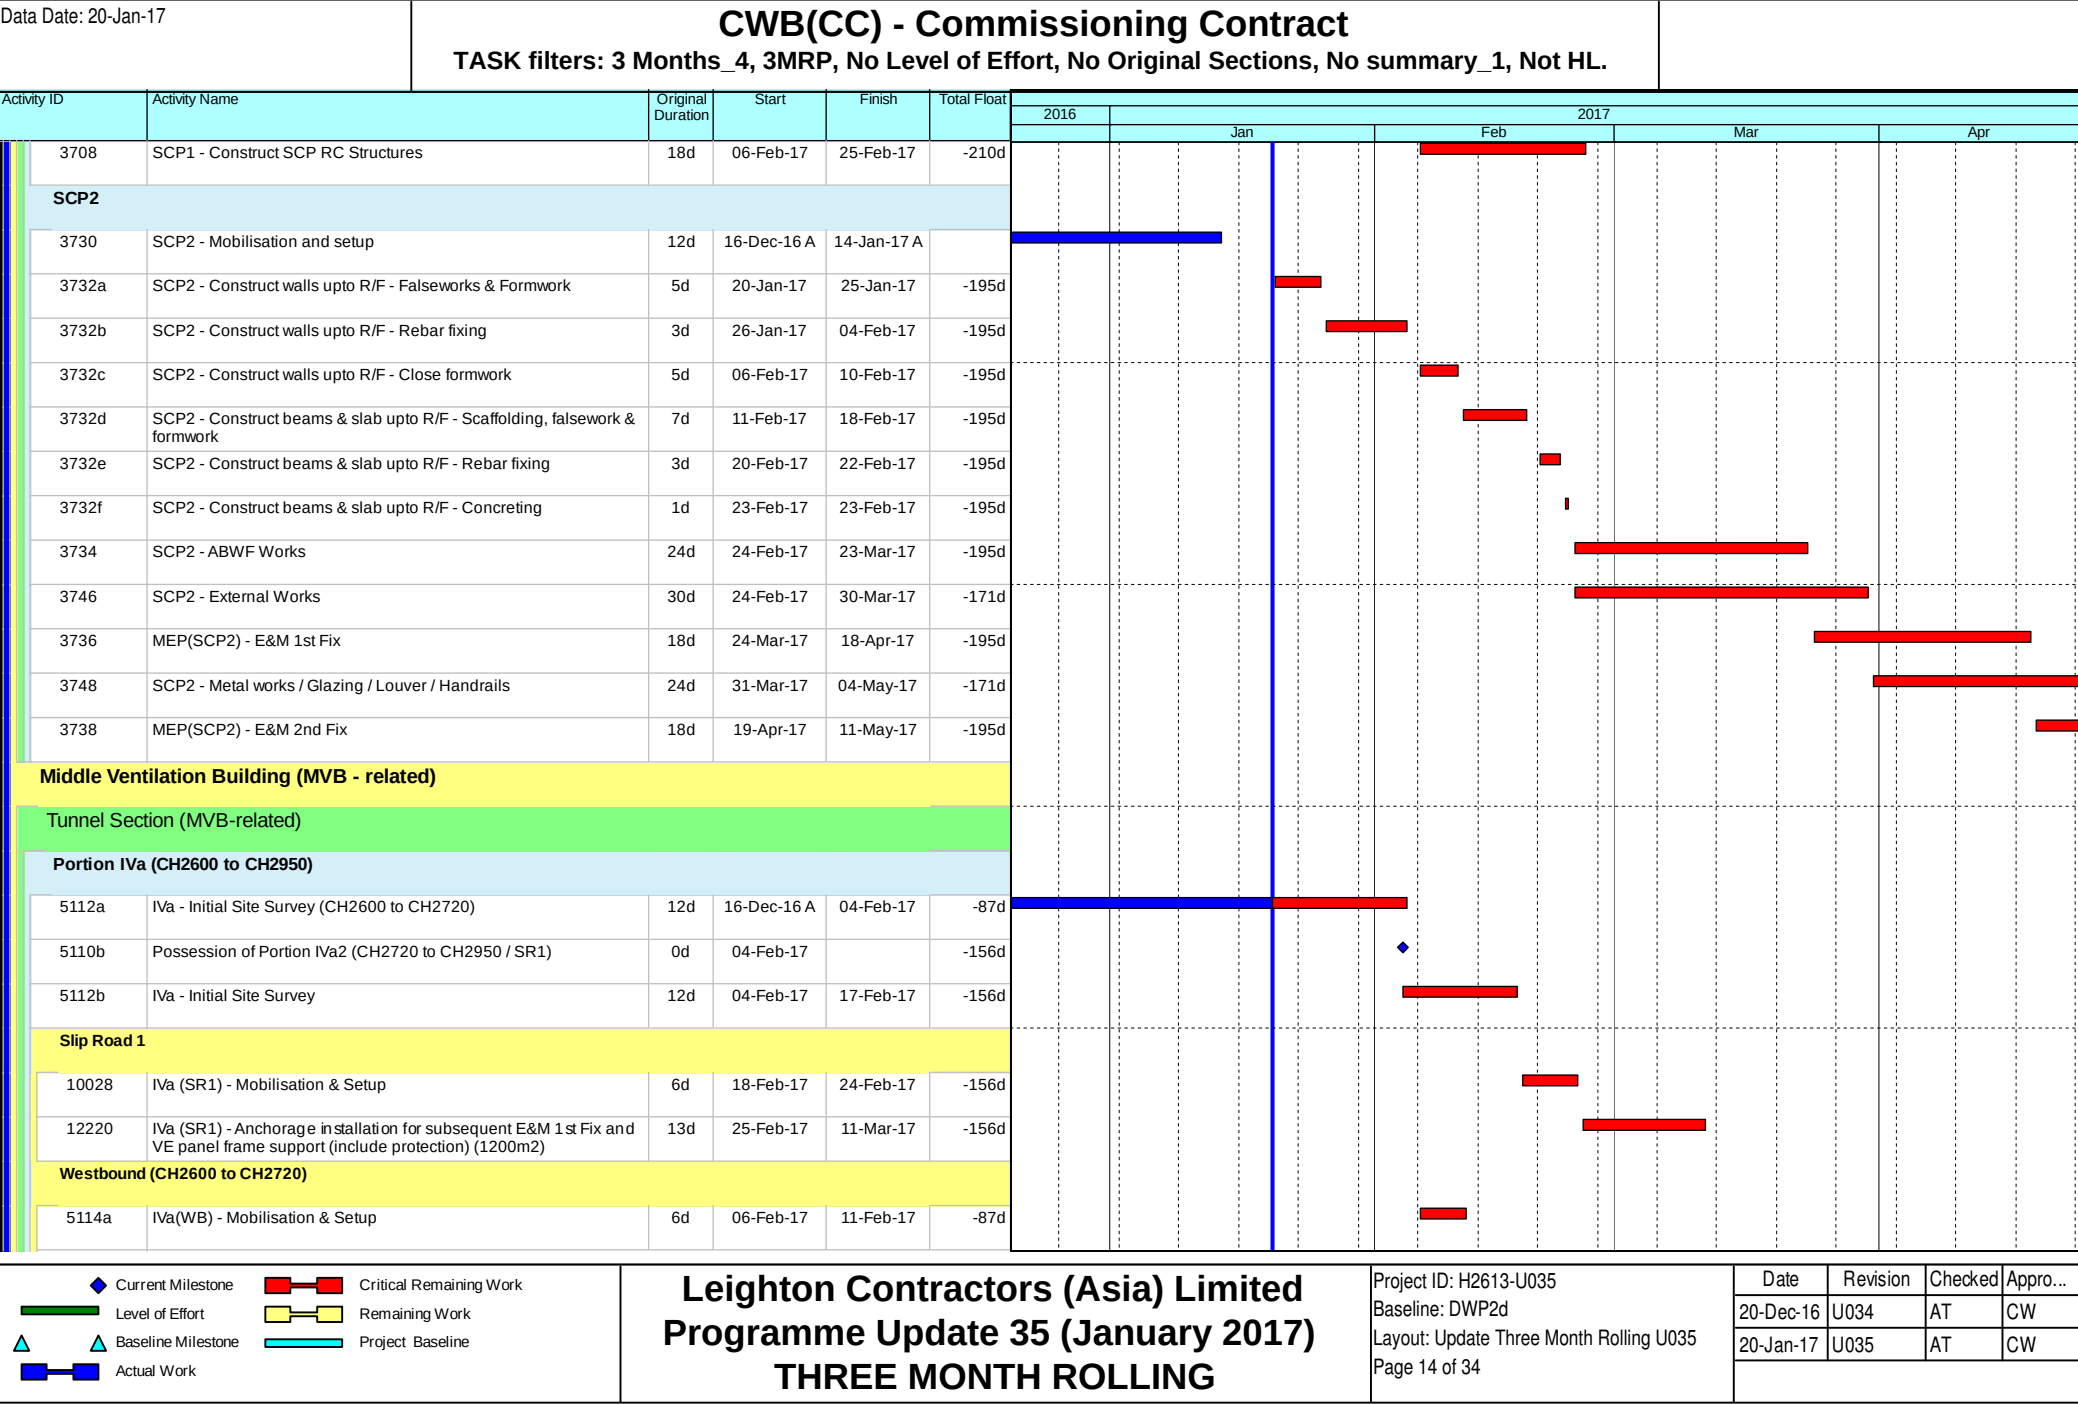


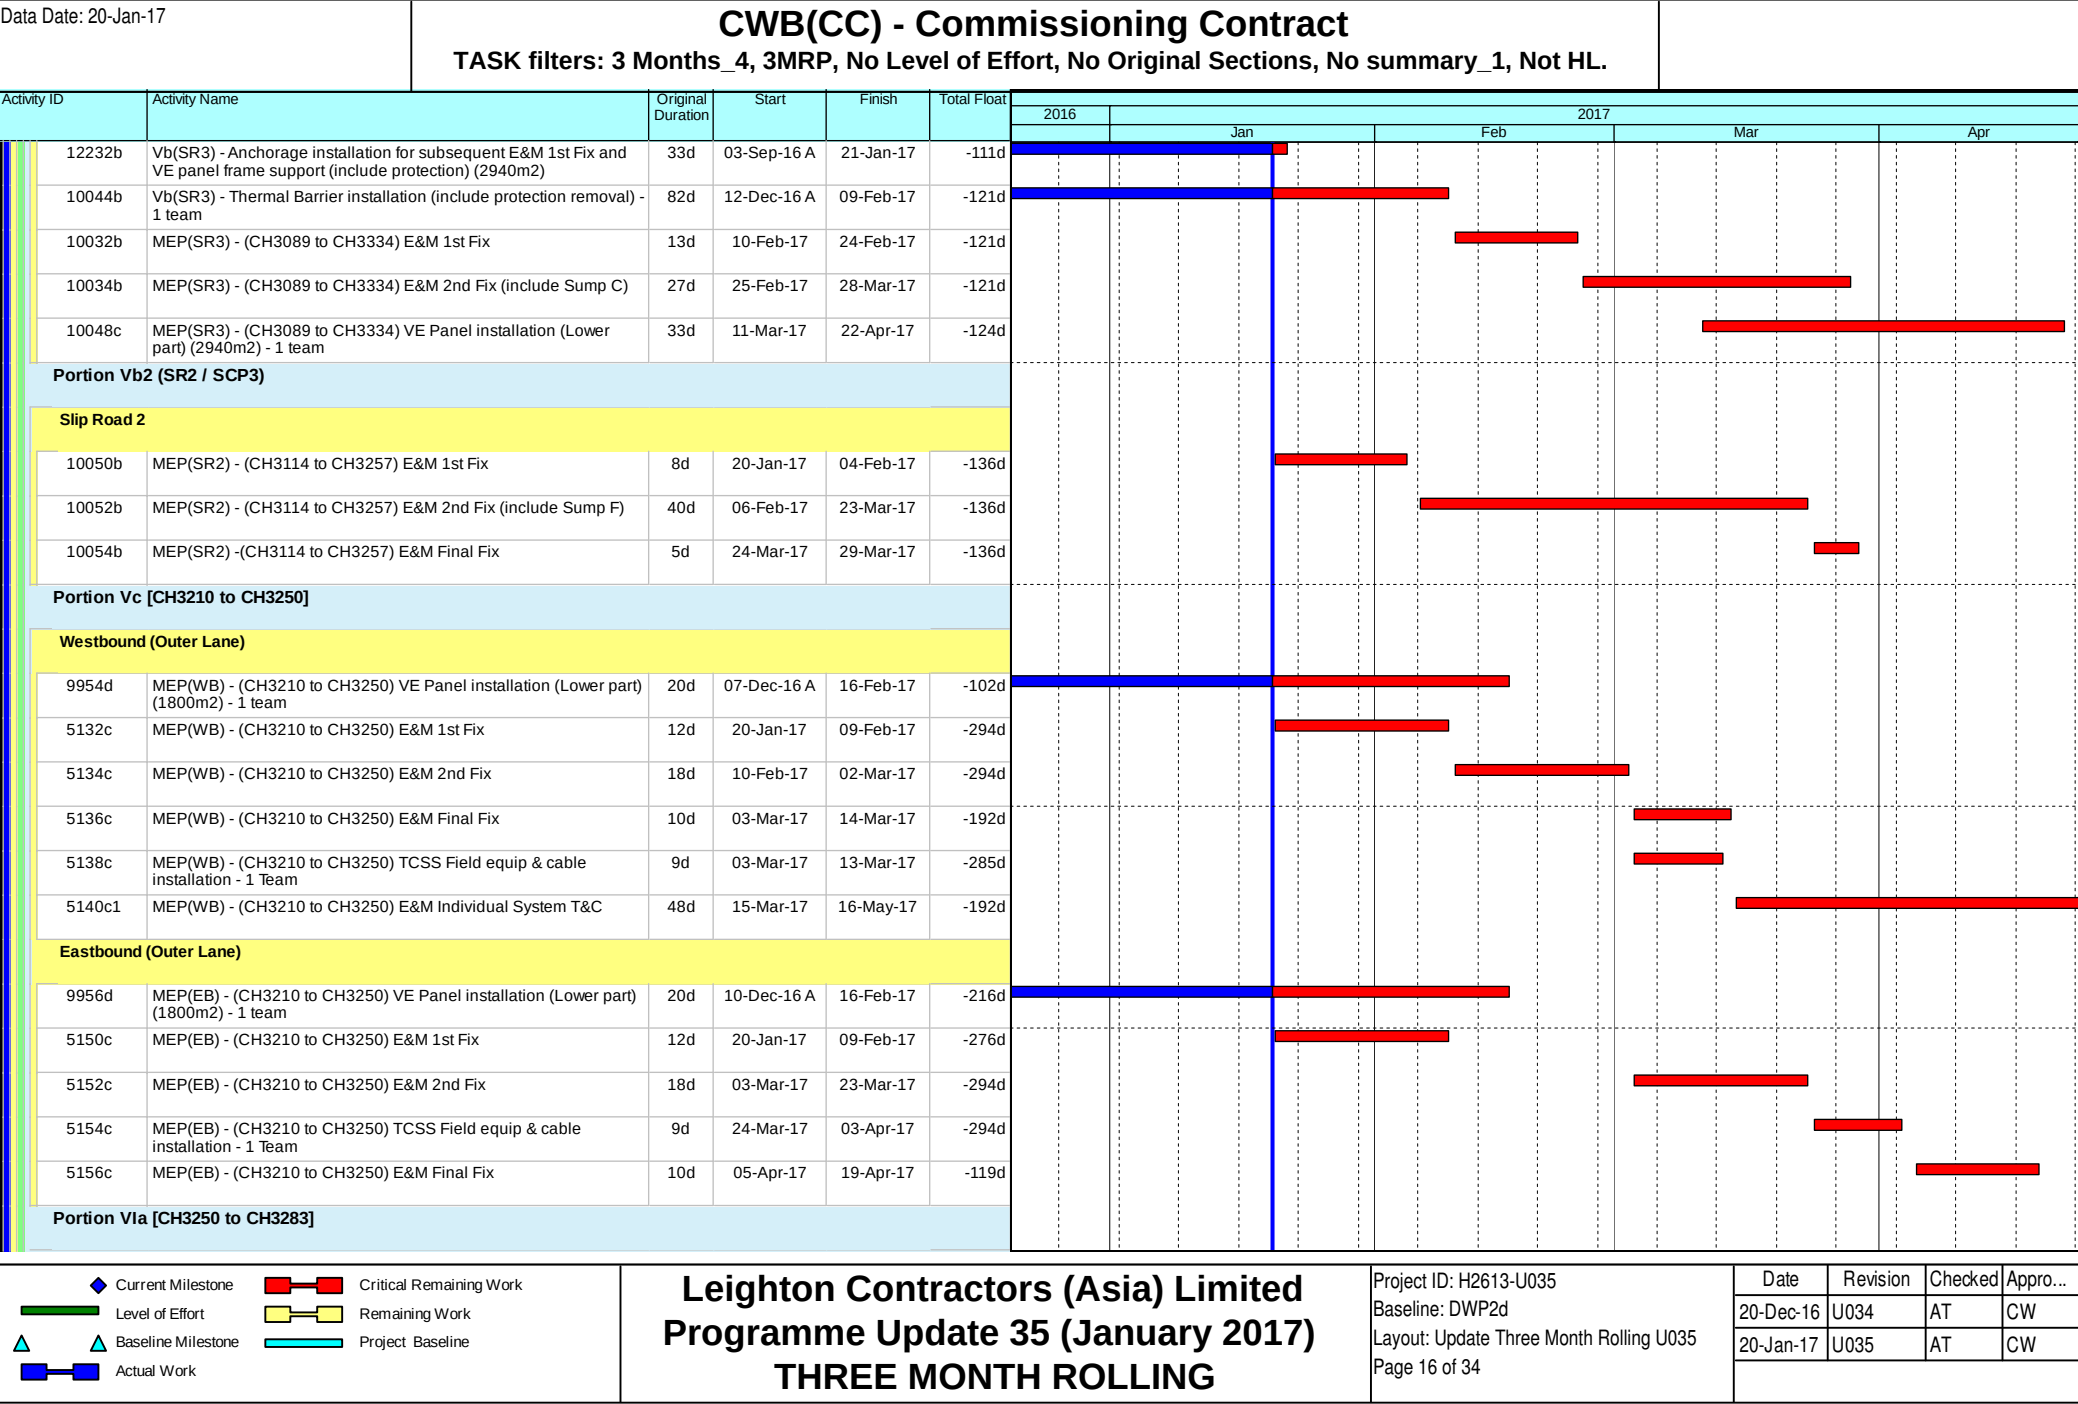


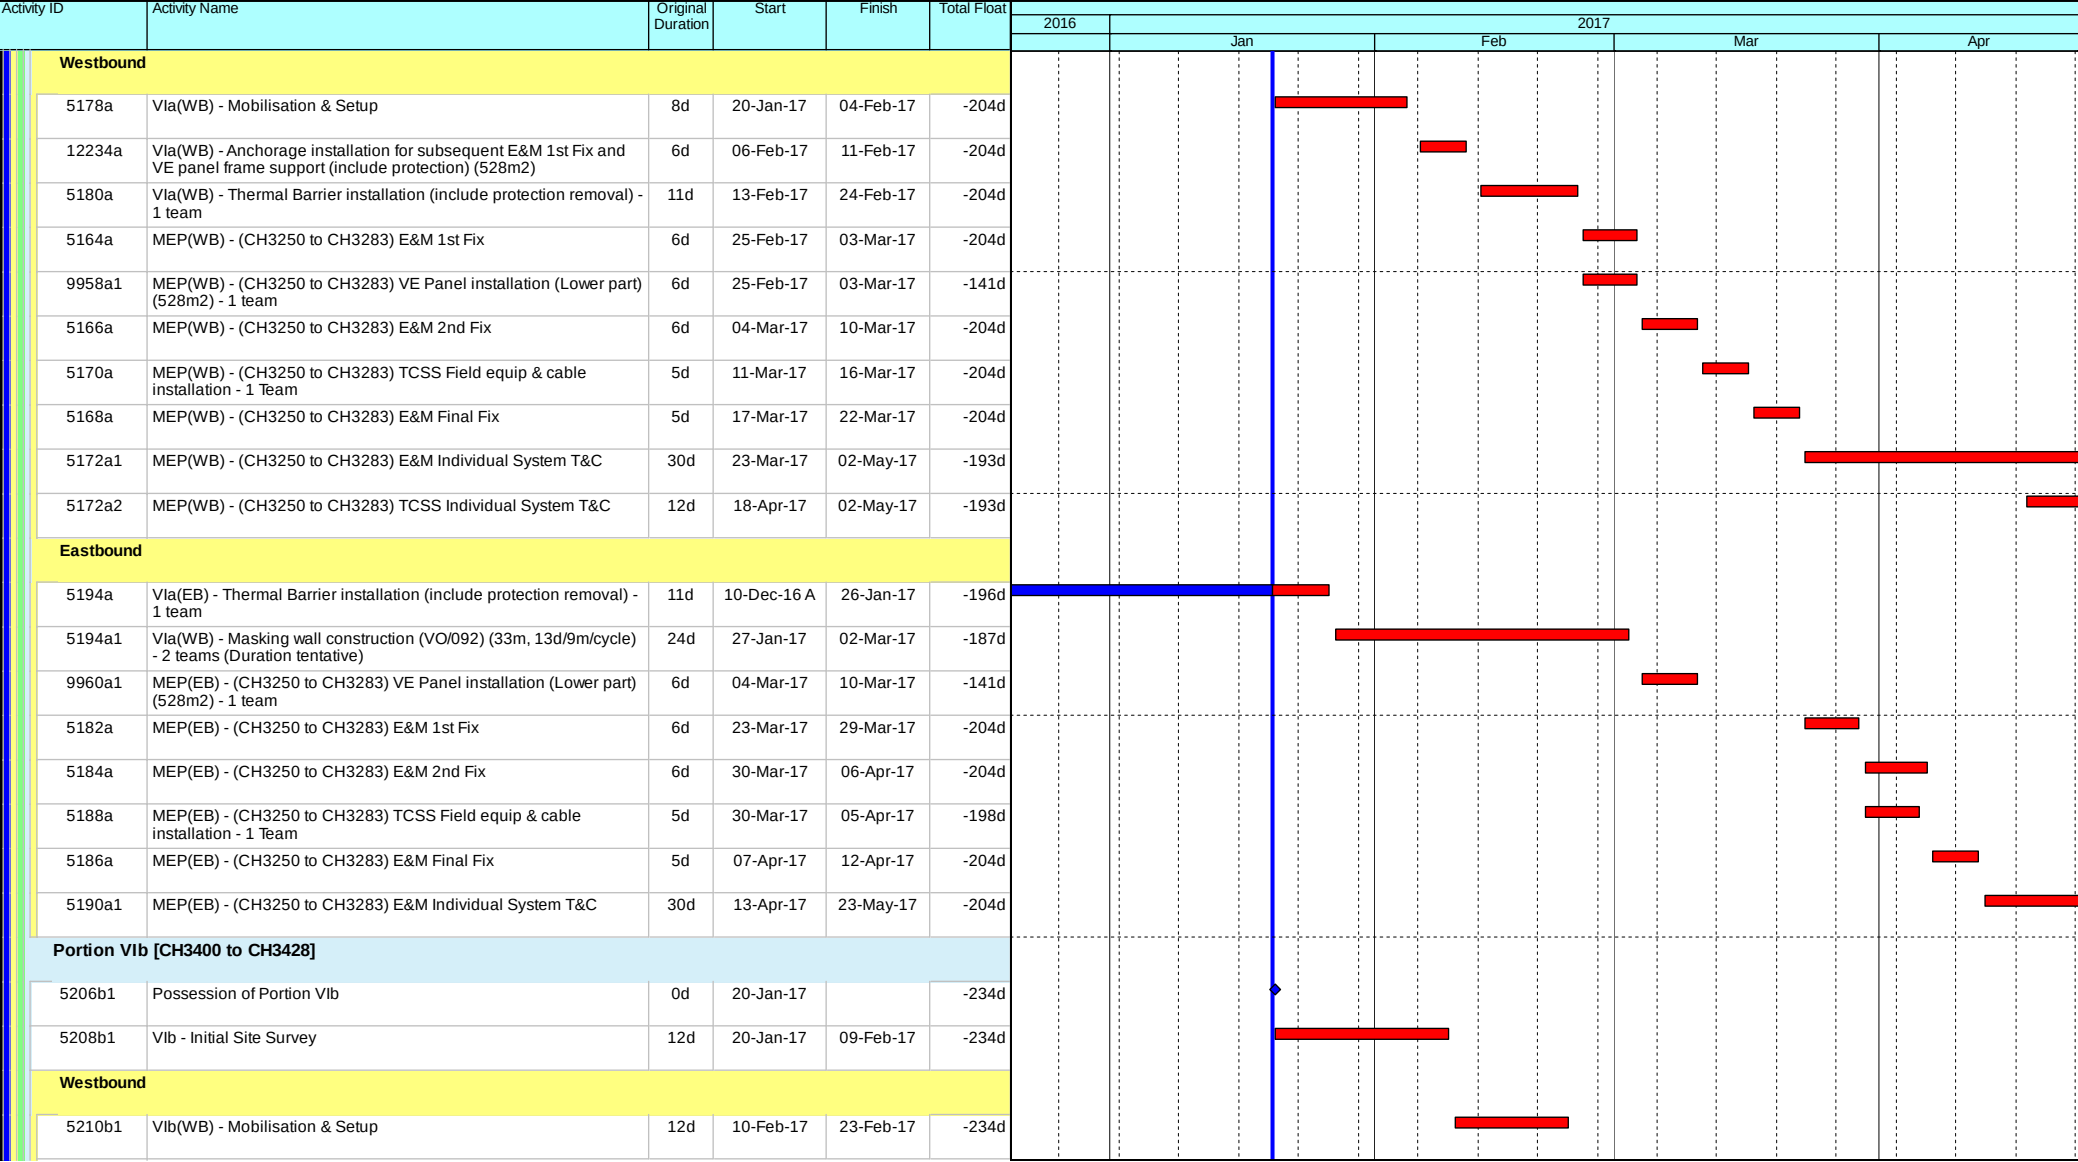


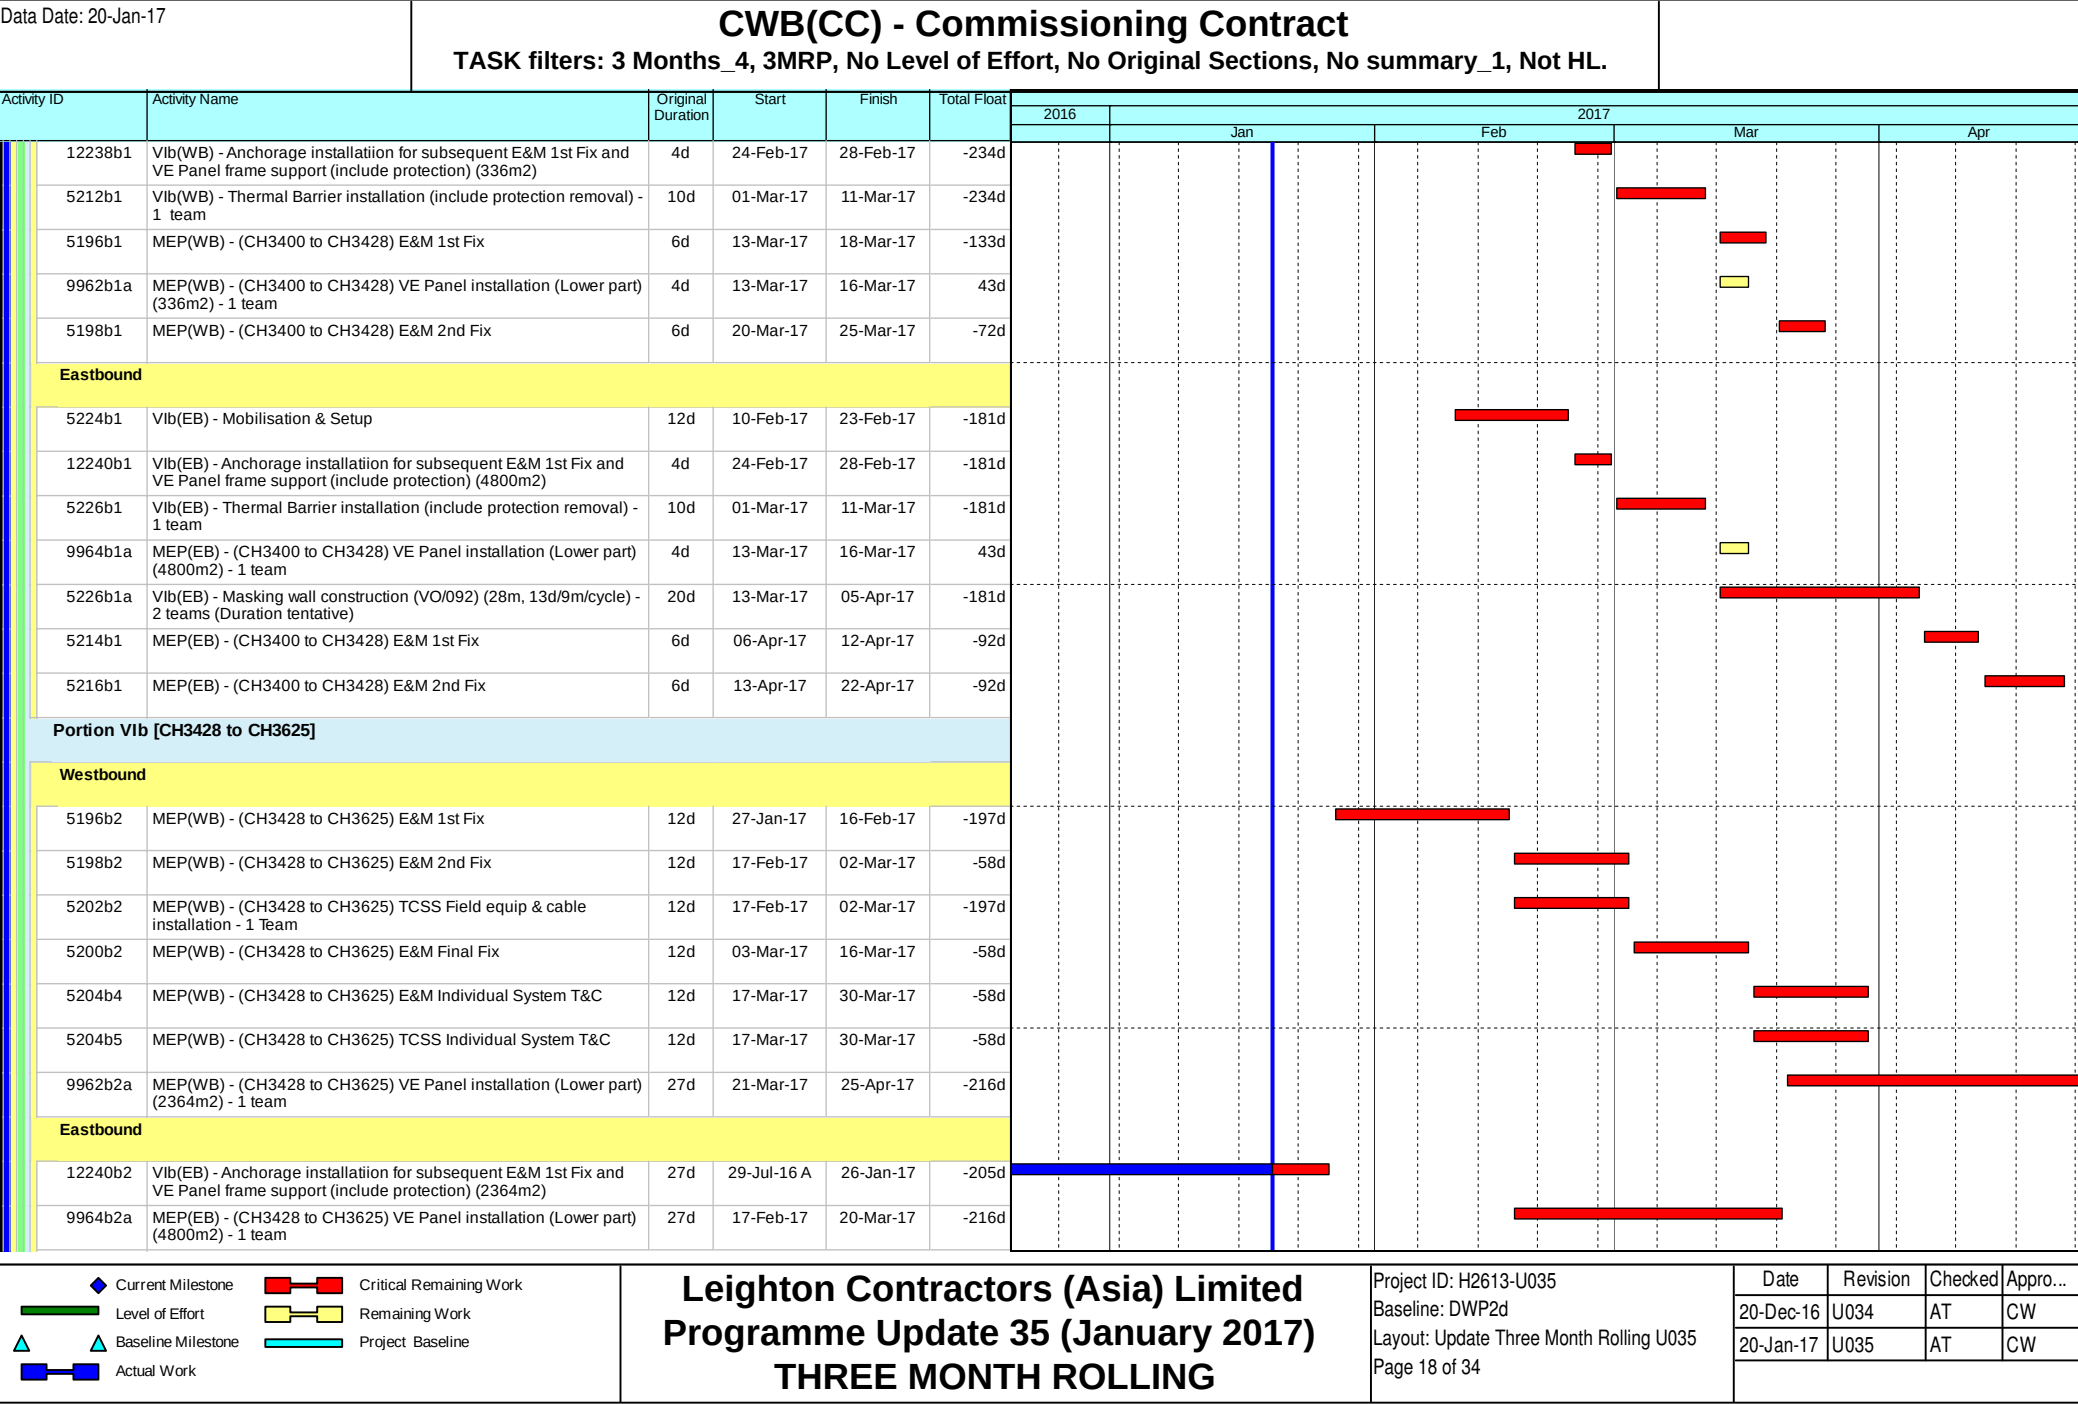


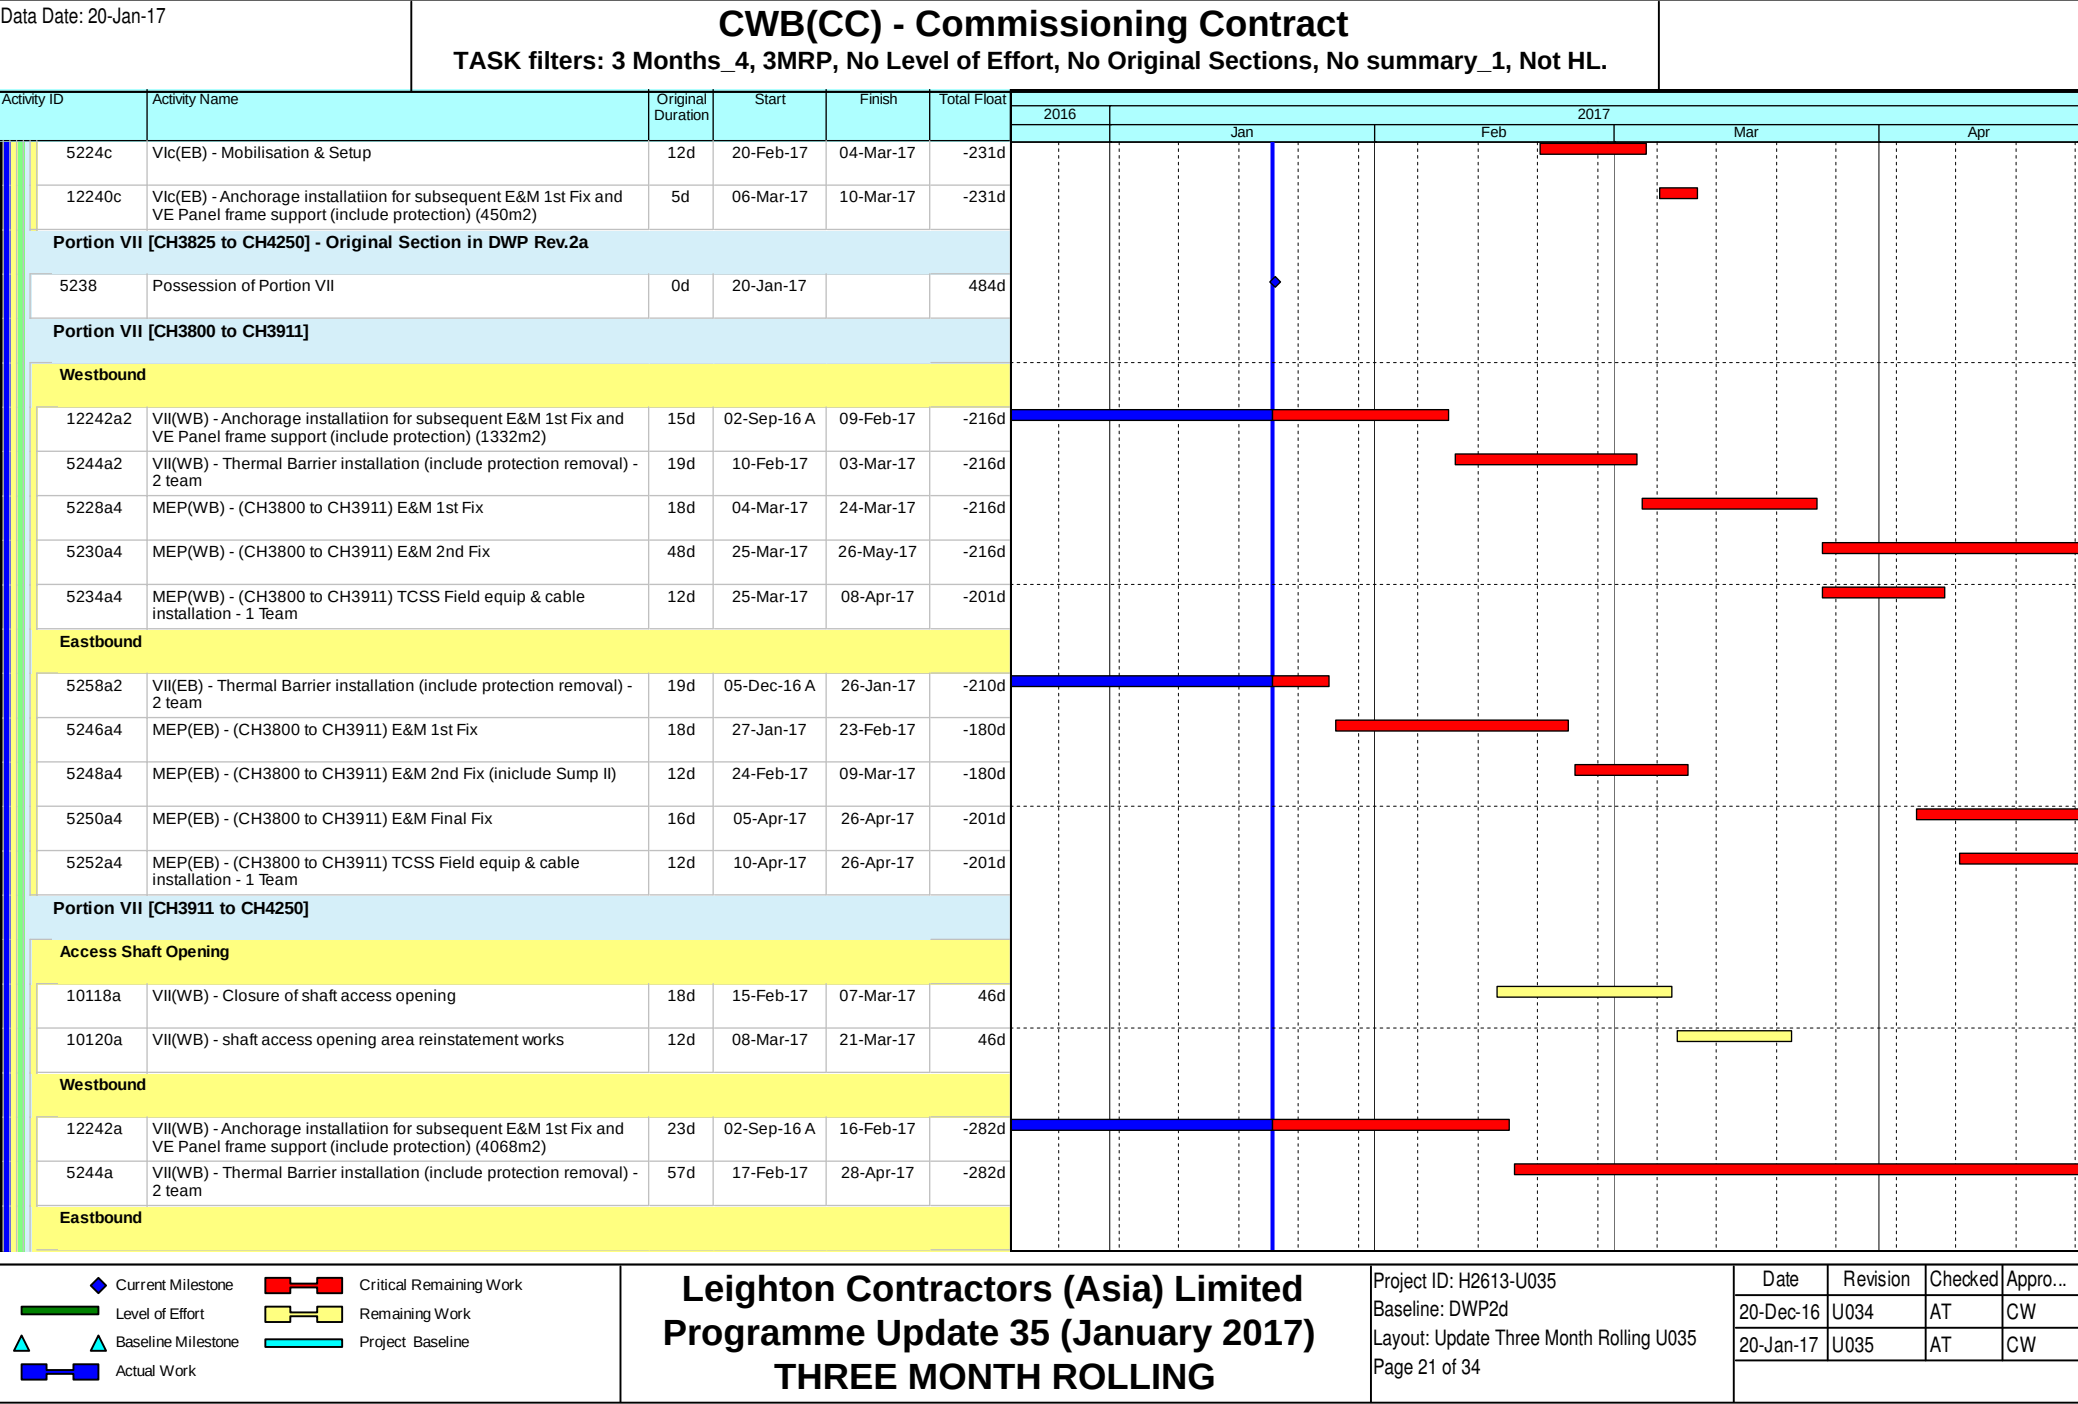


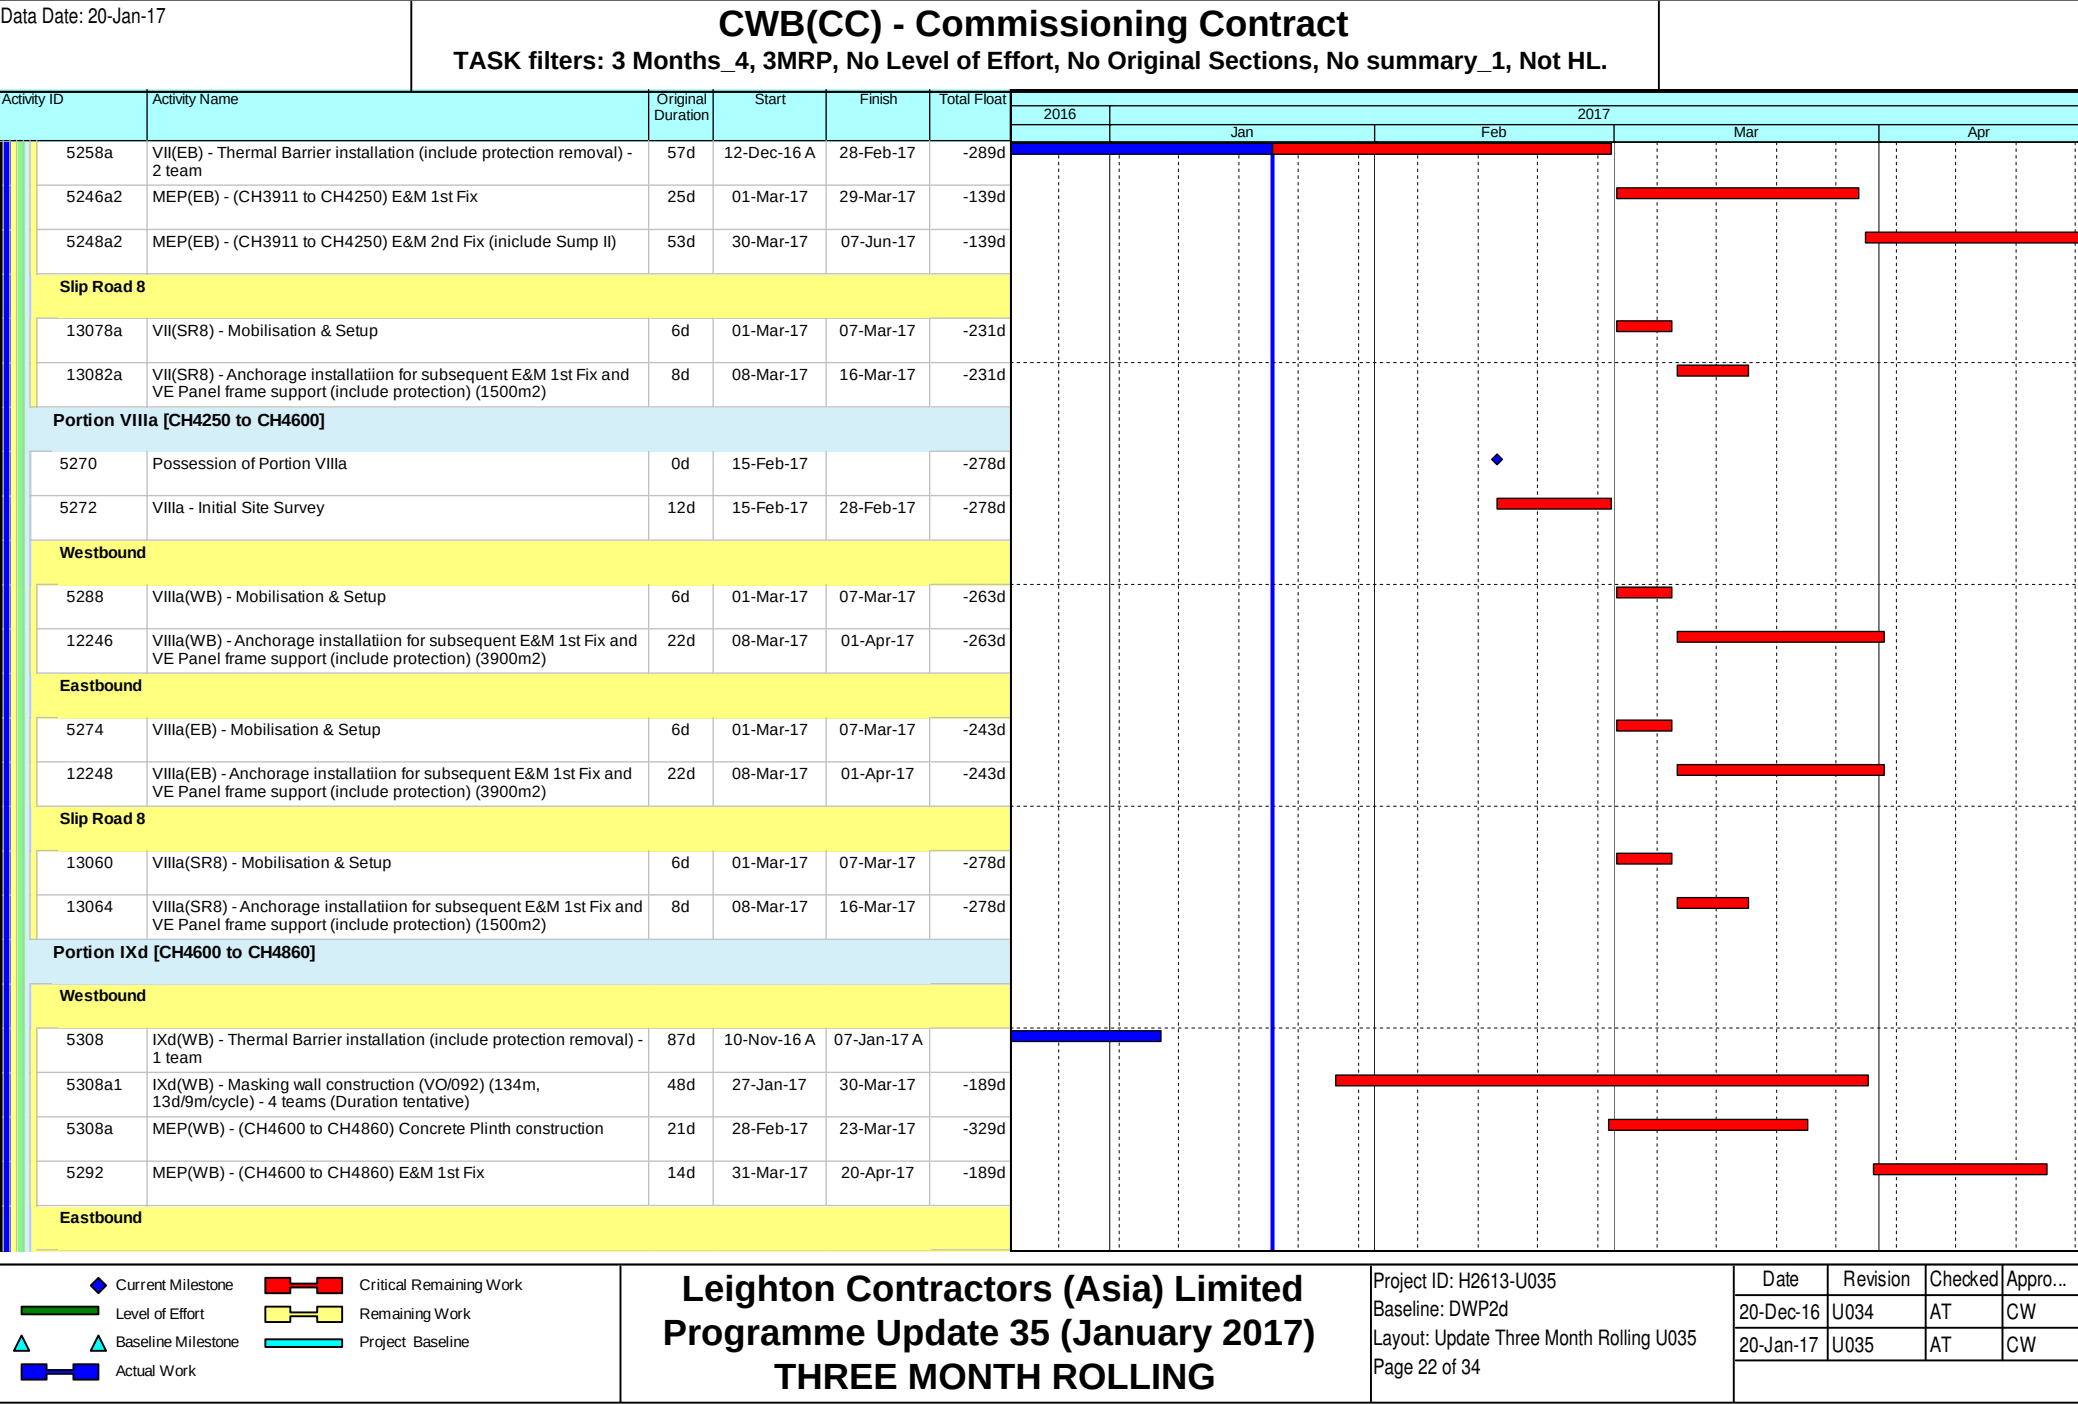


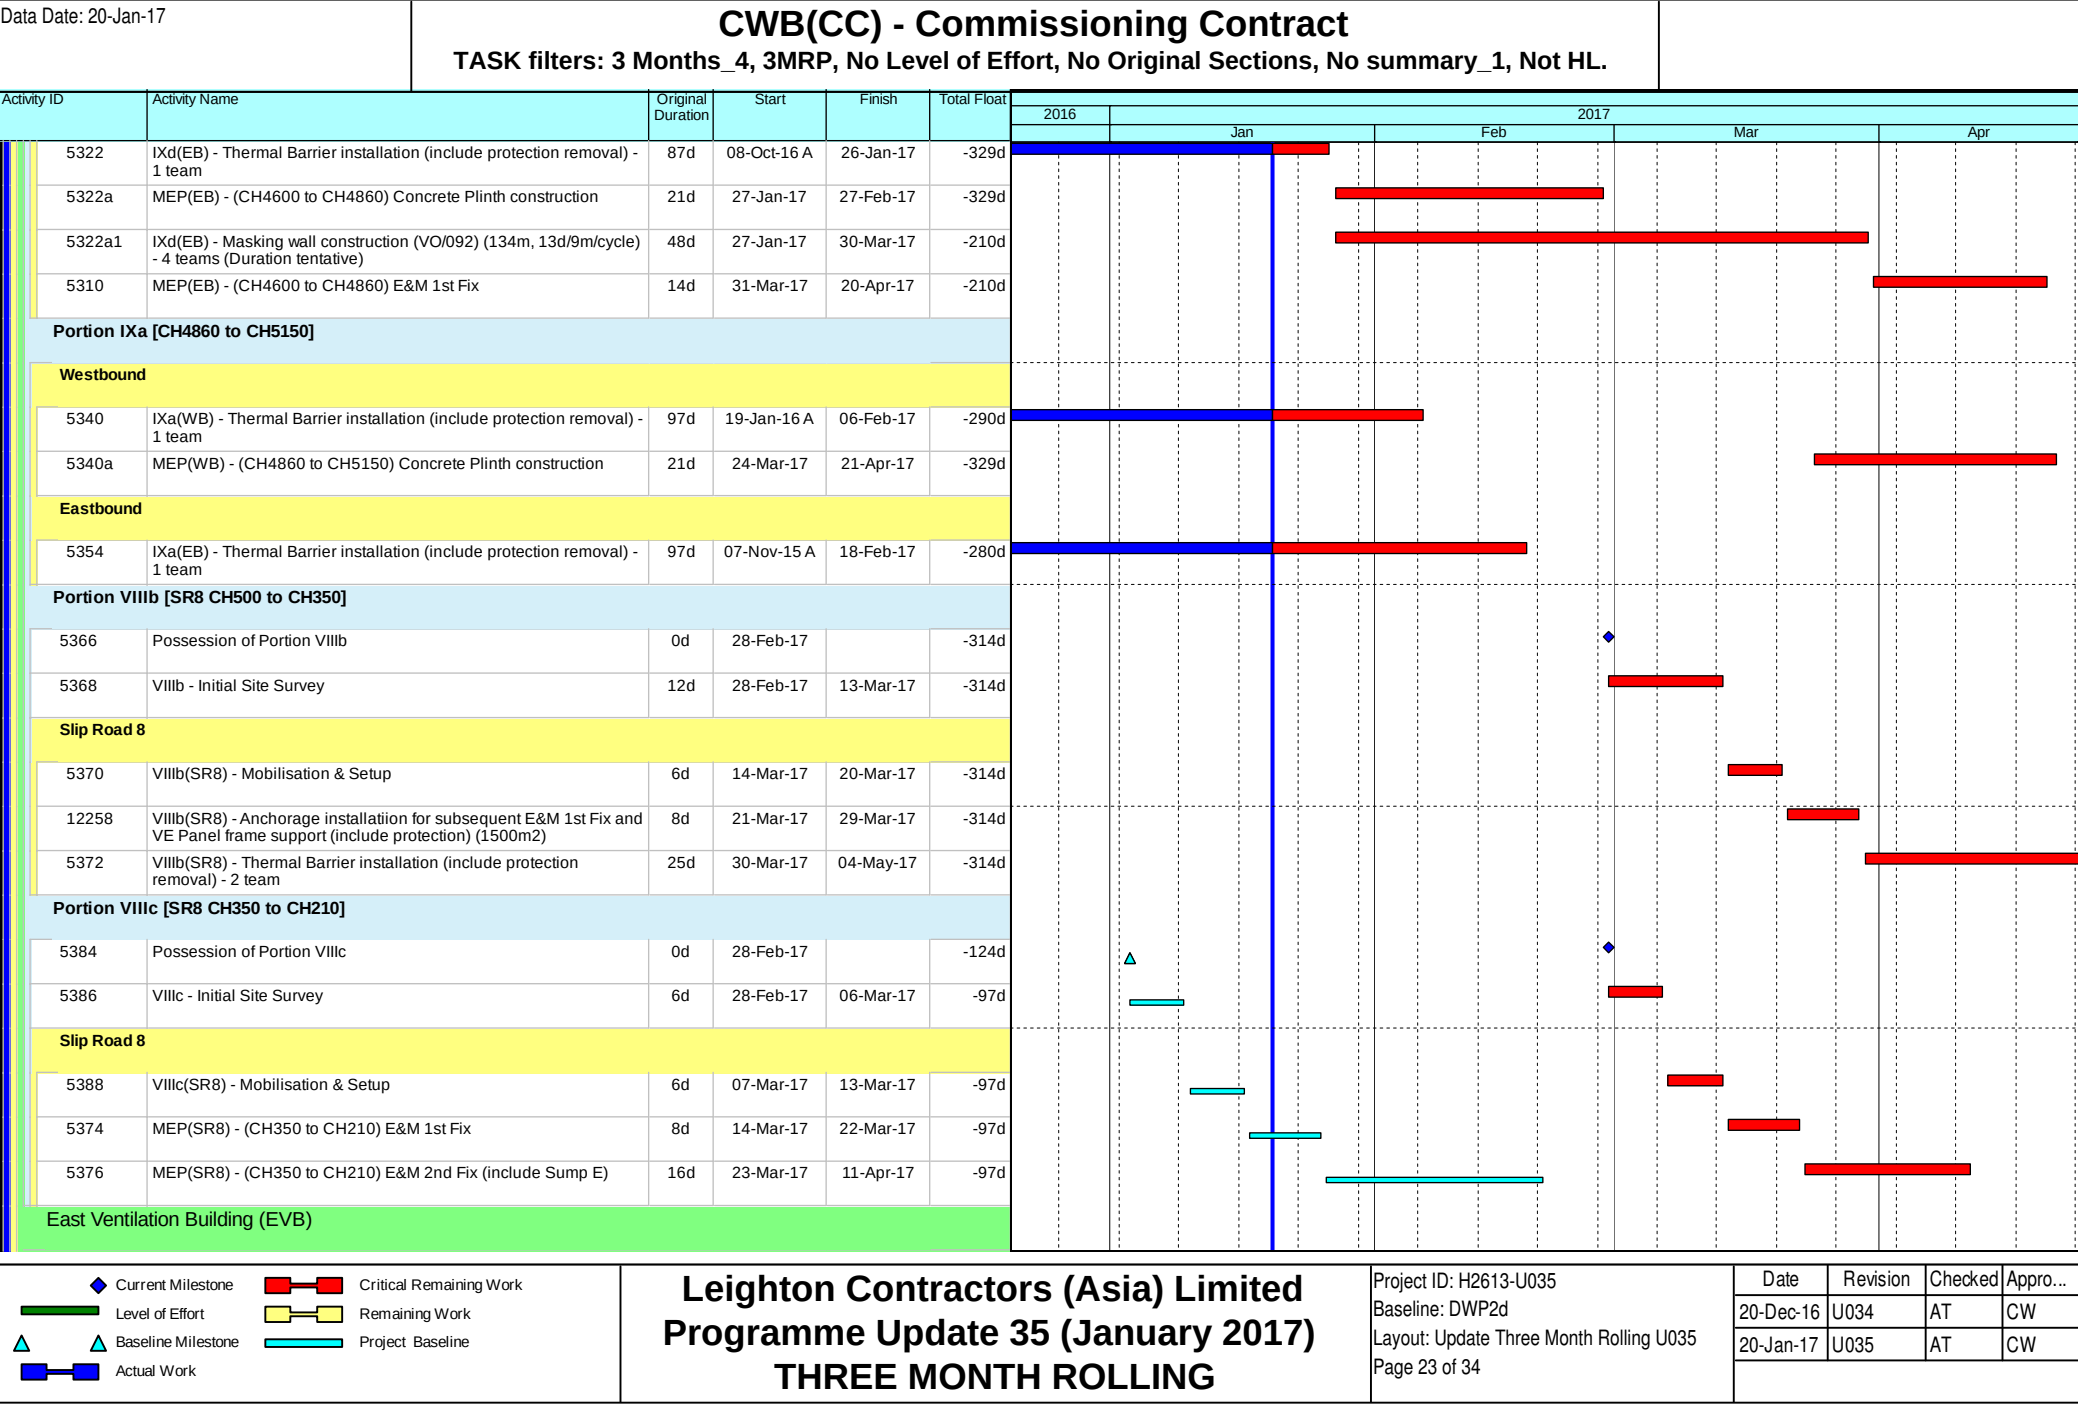

















Data Date: 20-Jan-17			CWB(CC) - Commissioning Contract															
			TASK filters: 3 Months_4, 3MRP, No Level of Effort, No Original Sections, No summary_1, Not HL.															
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float													
						2016	2017											
							Jan		Feb		Mar		Apr					
11524	EVB 1/F - Rebar fixing for column / walls	6d	27-Jan-17	09-Feb-17	-223d													
11526	EVB 1/F - Concrete for column / walls	1d	10-Feb-17	10-Feb-17	-223d													
11528	EVB 1/F - Scaffolding for beam & slab	8d	11-Feb-17	20-Feb-17	-223d													
11530	EVB 1/F - Decking / Formwork for beam & slab	8d	16-Feb-17	24-Feb-17	-223d													
11532	EVB 1/F - Rebar for beam & slab	12d	20-Feb-17	04-Mar-17	-223d													
11534	EVB 1/F - Close formwork for beam & slab	8d	06-Mar-17	14-Mar-17	-223d													
11536	EVB 1/F - Concrete beam & slab	1d	15-Mar-17	15-Mar-17	-223d													
L1-02 Irrigation Water Tank & Pump Room																		
11780	EVB 1/F (L1-02) - Internal walls / Cast-in items	1d	15-Mar-17	15-Mar-17	-161d													
11782	EVB 1/F (L1-02) - Plinths for F.S. Pump	6d	30-Mar-17	06-Apr-17	-173d													
11784	EVB 1/F (L1-02) - Water Tank	20d	07-Apr-17	05-May-17	-173d													
L1-05 MCC Room 1																		
11786	EVB 1/F (L1-08) - Internal walls / Cast-in items	1d	15-Mar-17	15-Mar-17	-171d													
L1-08 LV Switch Room																		
11568	EVB 1/F (L1-08) - Internal walls / Cast-in items	1d	15-Mar-17	15-Mar-17	-159d													
L1-09 MCC Room 2																		
11788	EVB 1/F (L1-08) - Internal walls / Cast-in items	1d	15-Mar-17	15-Mar-17	-159d													
1/F (GL A-D) Other Rooms / Corridors / Staircase																		
11580	EVB 1/F (GL A-D) - Remaining Internal walls / Cast-in items	1d	15-Mar-17	15-Mar-17	-123d													
11582	EVB 1/F (GL A-D) - Plinths / R.C. curbs	12d	07-Apr-17	24-Apr-17	-66d													
MEP & ABWF Works																		
Basement 2 - APS Auxiliary Room / APS Plant Area 1 / APS Plant Area 2 / APS Plant Area 3																		
3556	APS(EVB) - ABWF works	12d	30-Mar-17	13-Apr-17	-216d													
12292	APS(EVB) - E&M 1st fixing	24d	18-Apr-17	17-May-17	-216d													
Basement 2 - Sump Pump Room (B2-12)																		
										</								

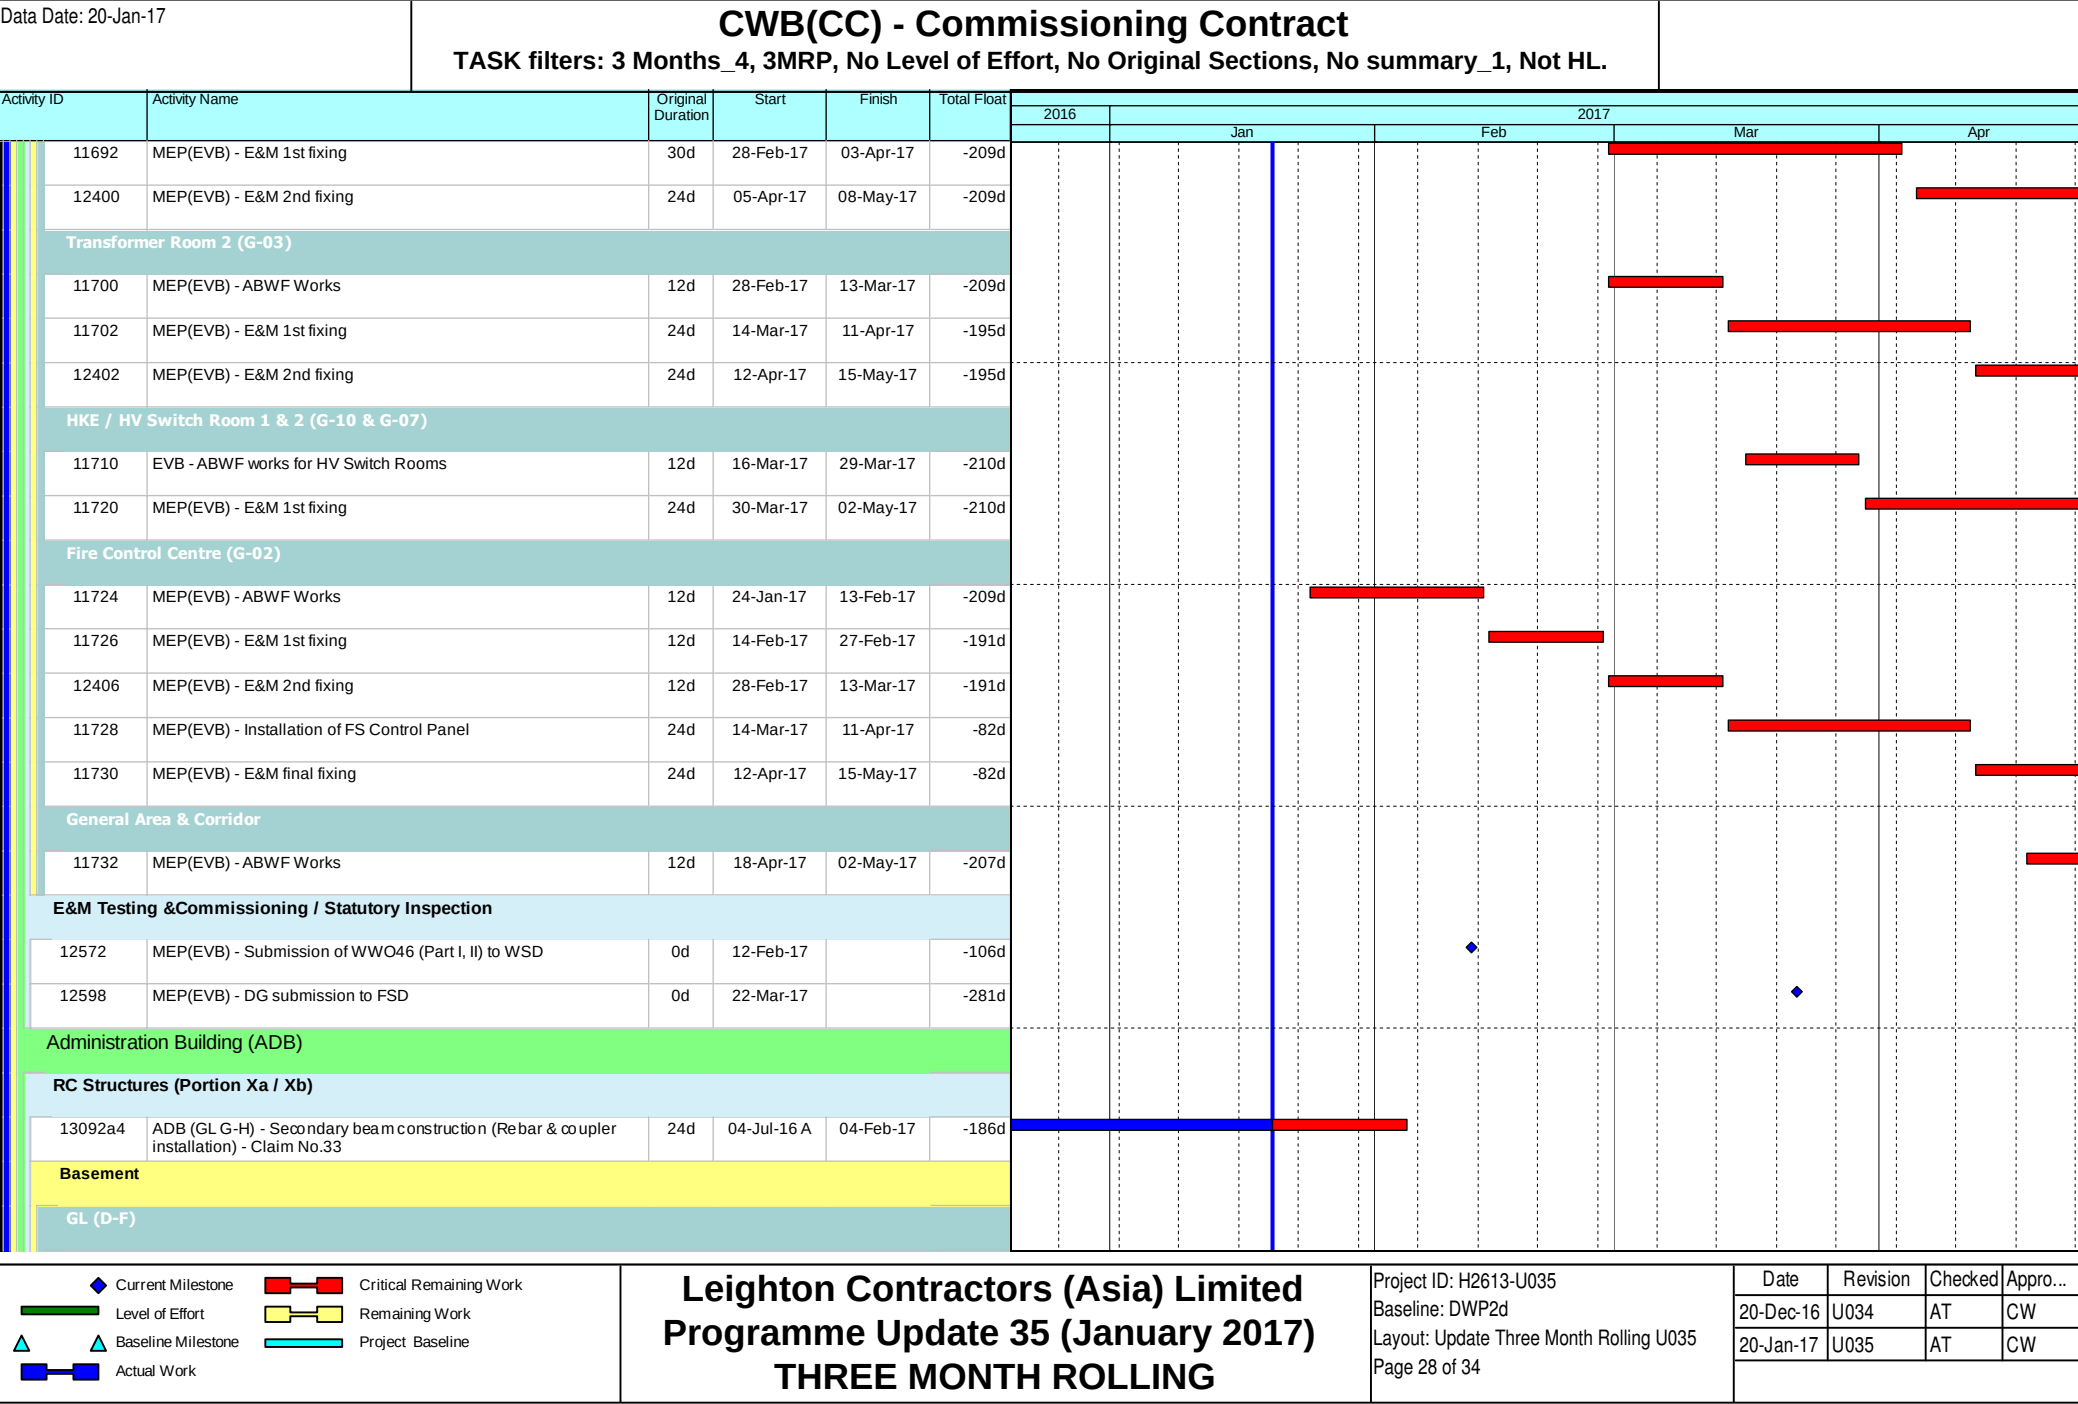

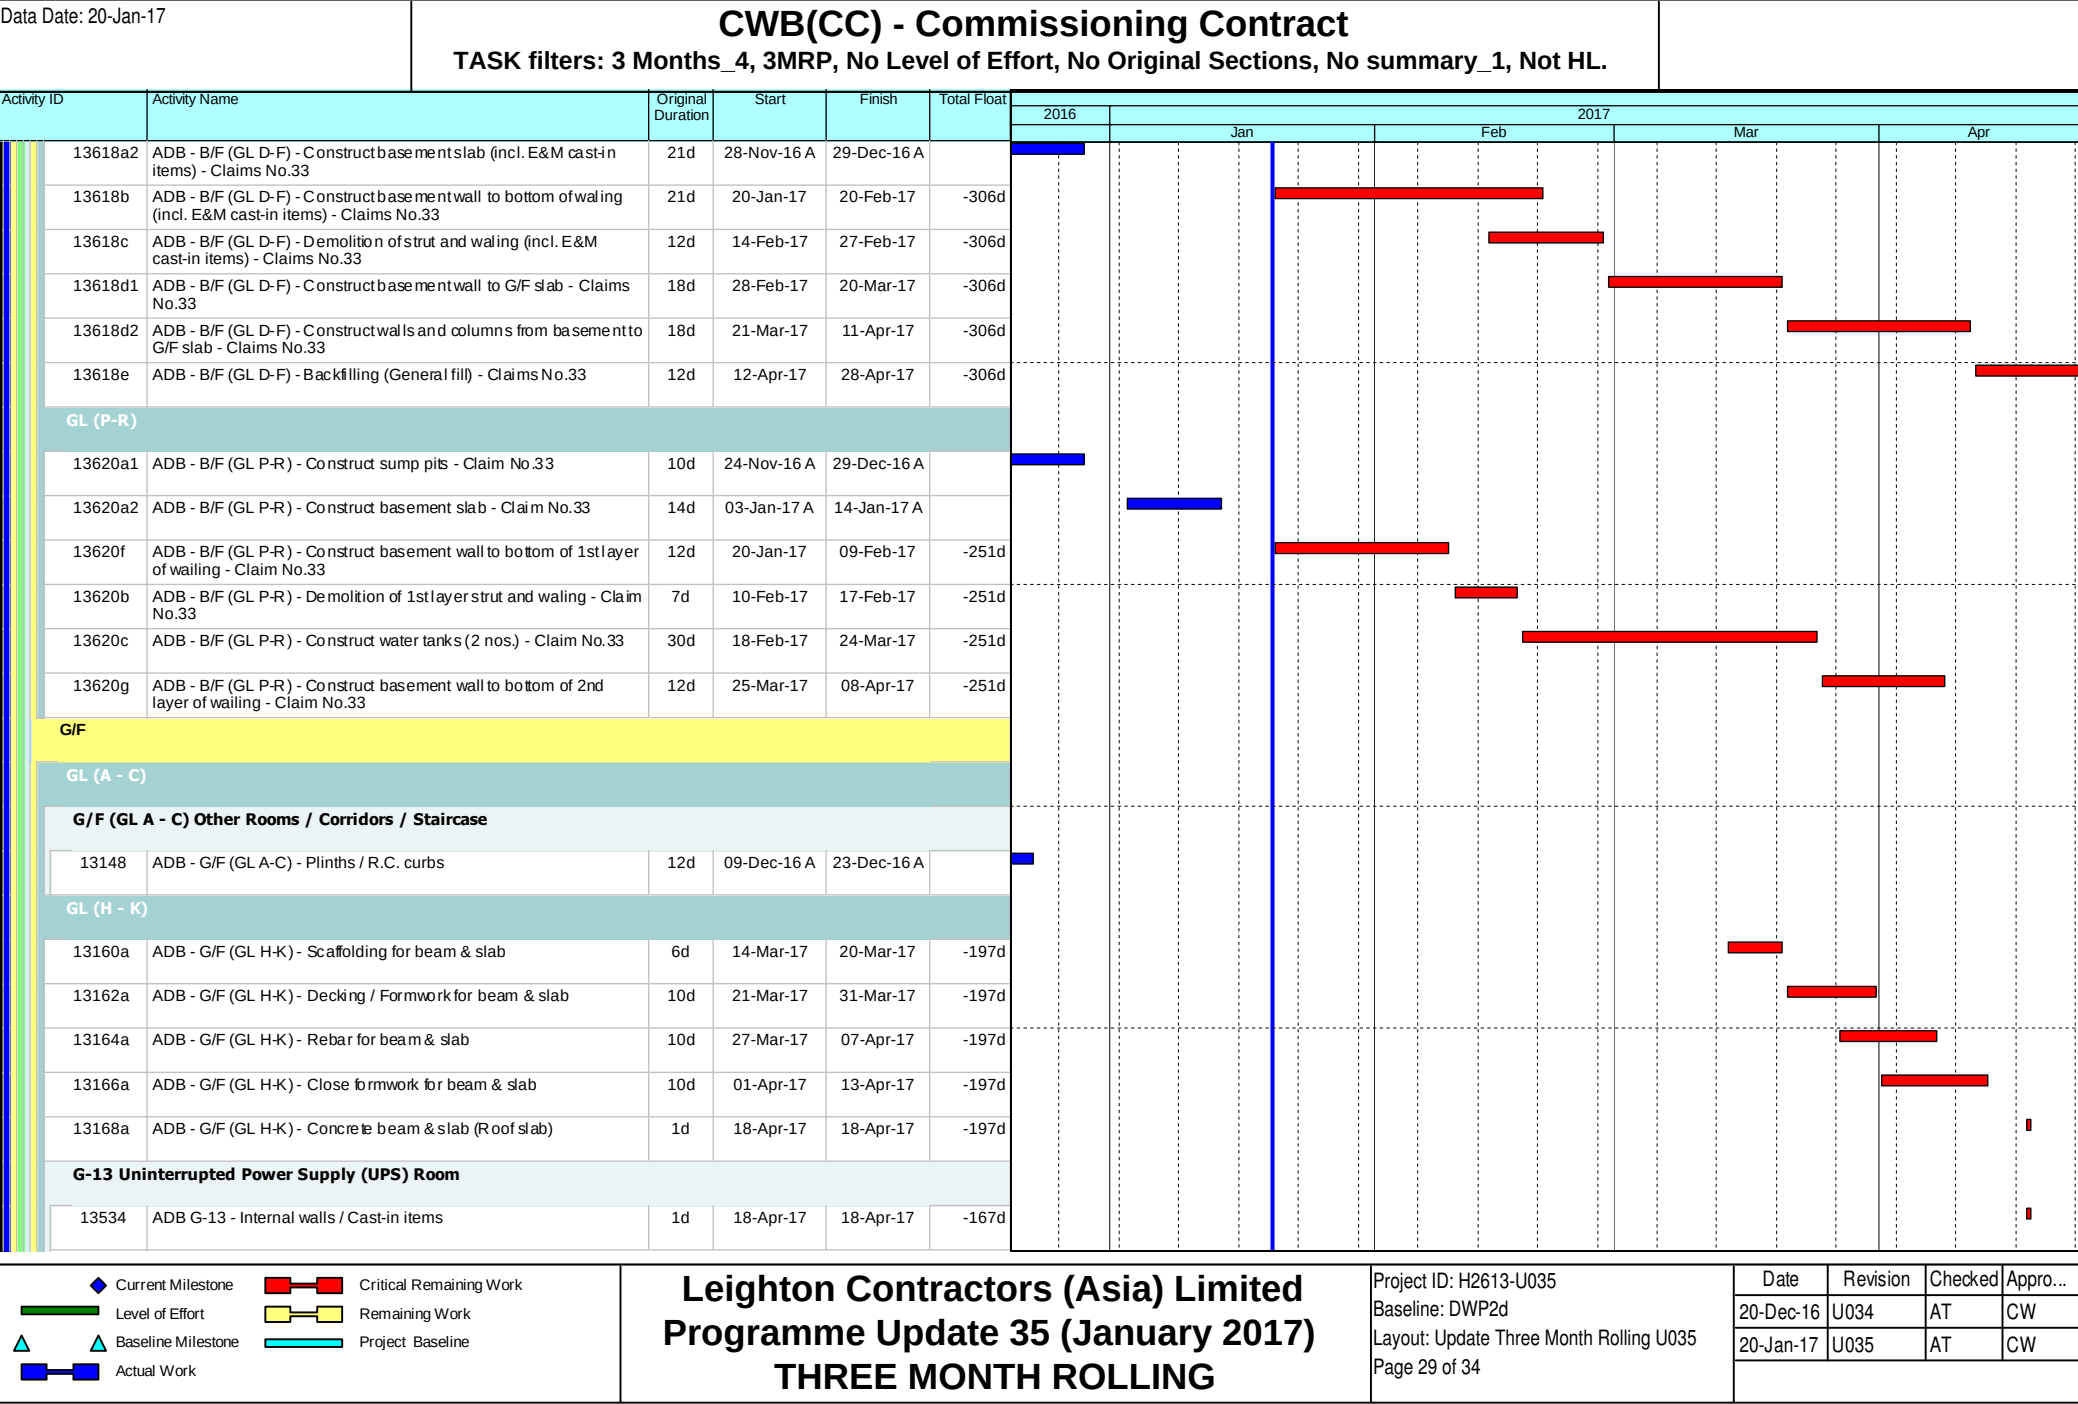

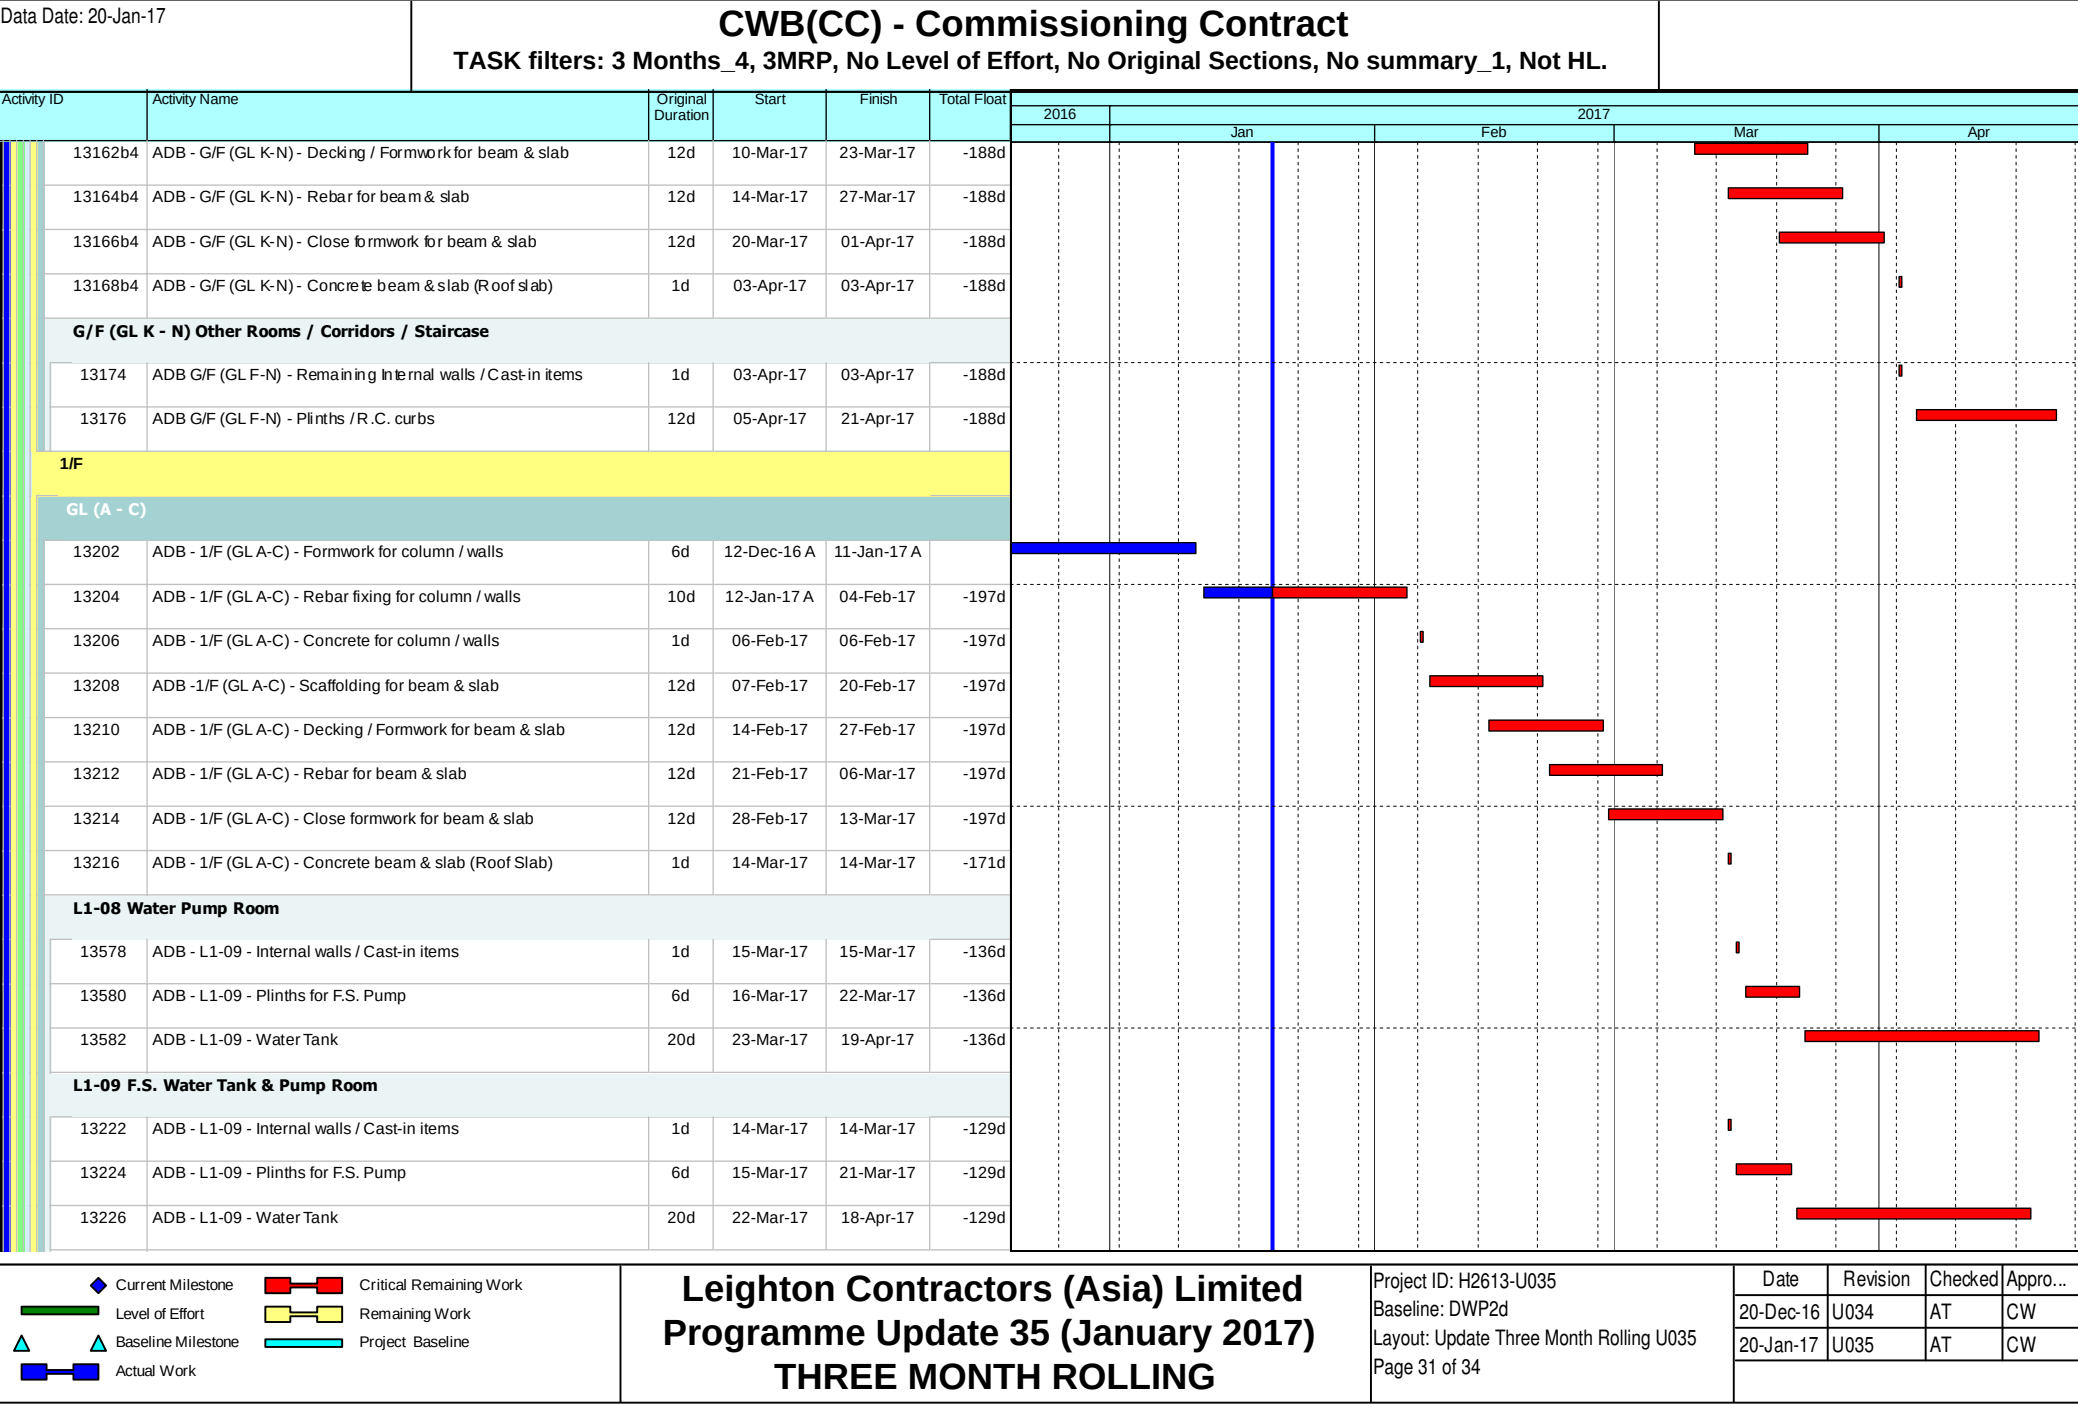

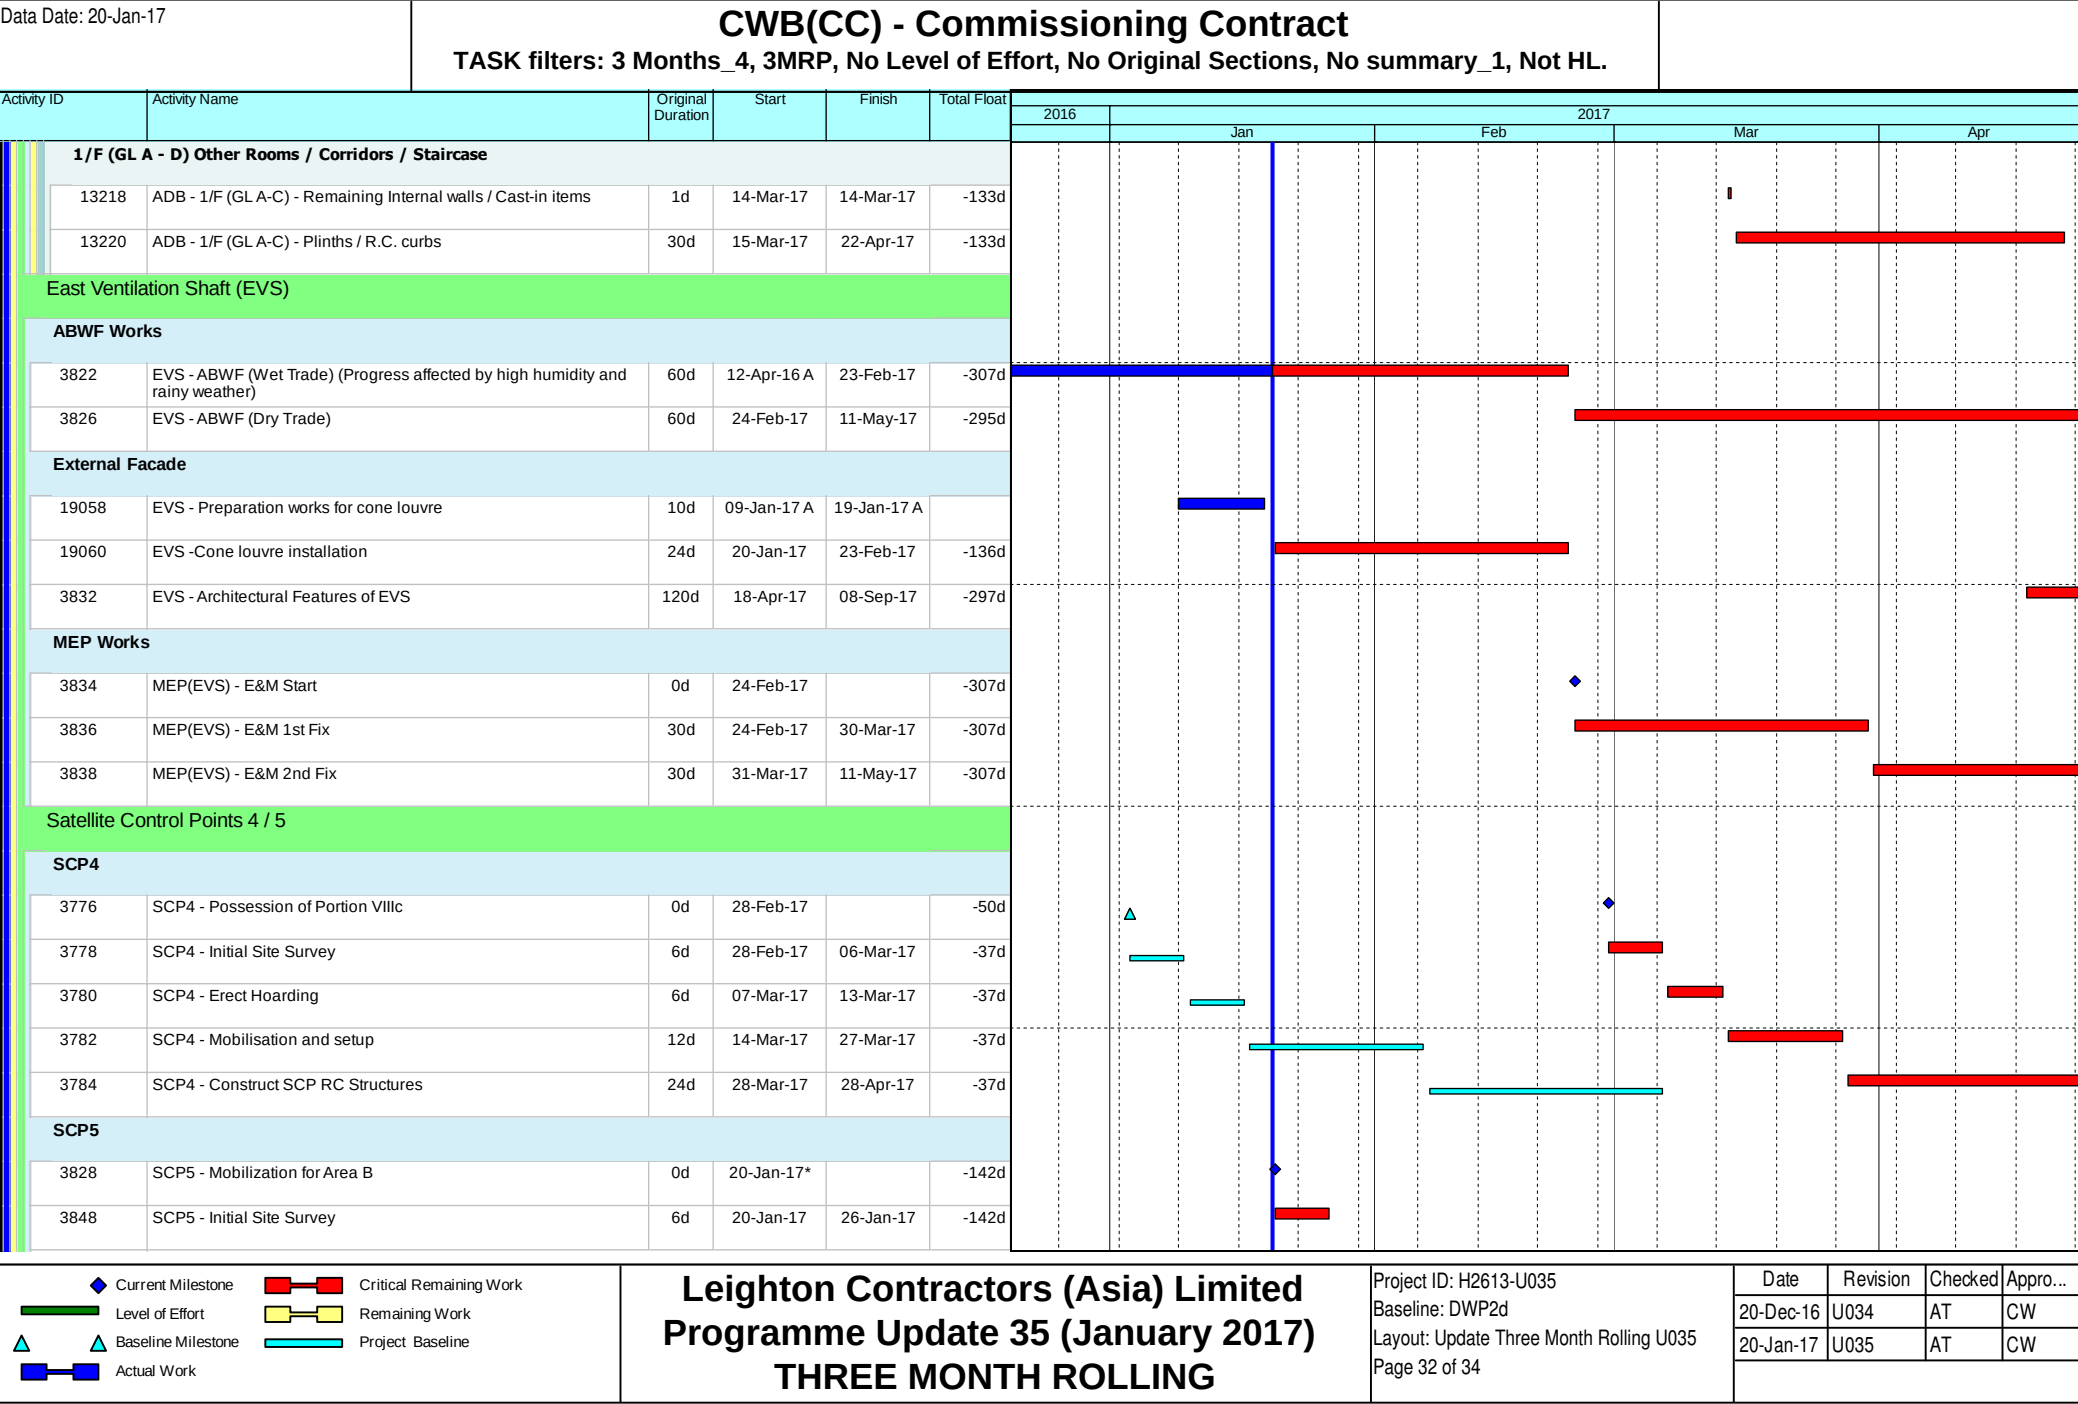

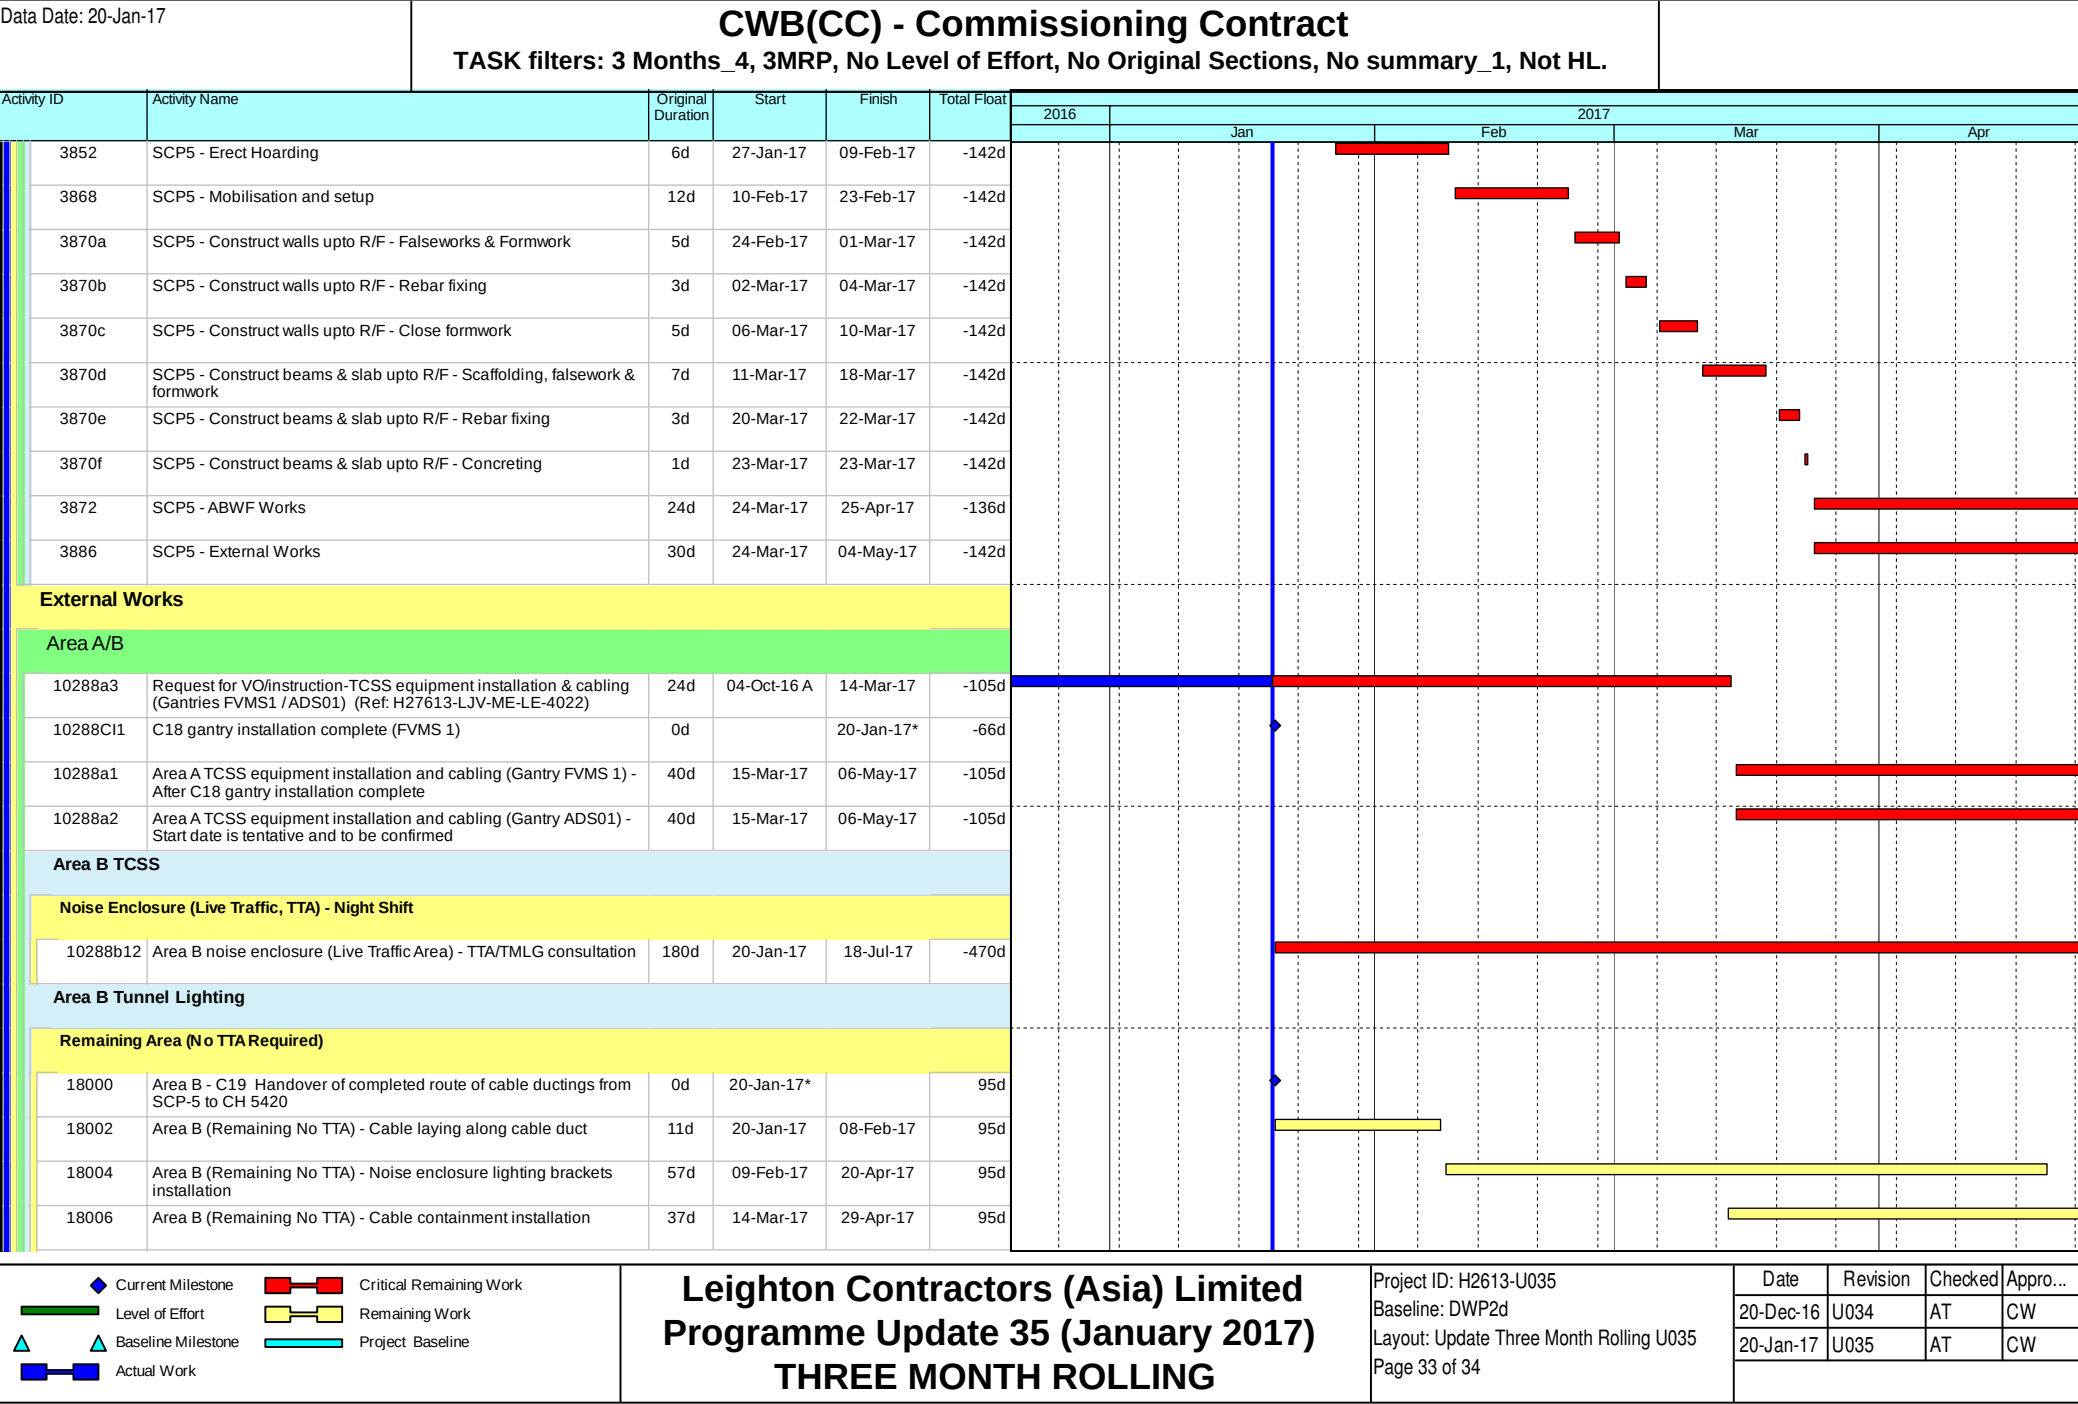

Data Date: 20-Jan-17		CWB(CC) - Commissioning Contract				TASK filters: 3 Months_4, 3MRP, No Level of Effort, No Original Sections, No summary_1, Not HL.												
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float													
						2016	2017											
							Jan			Feb			Mar			Apr		
Remaining Area (TTA Required)																		
EastBound																		
19000	Area B - TTA Approved	0d	20-Jan-17*		80d													
19002	Area B (Remaining need TTA) - Noise enclosure lighting brackets installation	43d	20-Jan-17	17-Mar-17	80d													
19004	Area B (Remaining need TTA) - Cable containment installation	17d	18-Mar-17	07-Apr-17	80d													
19006	Area B (Remaining need TTA) - Noise enclosure lighting installation	3d	08-Apr-17	11-Apr-17	80d													
19008	Area B (Remaining need TTA) - Lighting power cable laying (High Level)	12d	12-Apr-17	28-Apr-17	80d													
WestBound																		
19014	Area B - TTA Approved	0d	20-Jan-17*		58d													
19016	Area B (Remaining need TTA) - Noise enclosure lighting brackets installation	53d	20-Jan-17	29-Mar-17	58d													
19018	Area B (Remaining need TTA) - Cable containment installation	29d	30-Mar-17	09-May-17	58d													

Current Milestone

Level of Effort

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 35 (January 2017)

THREE MONTH ROLLING

Project ID: H2613-U035

Baseline: DWP2d

Layout: Update Three Month Rolling U035

Page 34 of 34


Date	Revision	Checked	Appro...
20-Dec-16	U034	AT	CW
20-Jan-17	U035	AT	CW

Data Date: 20-Apr-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017											
						Apr			May			Jun			Jul		
Update 2017-04-20 CWB(CC) - Commissioning Contract (DWP R2d)																	
PRELIMINARIES AND GENERAL REQUIREMENTS																	
Salient Key Dates and Milestones																	
Contract Key Dates																	
KD003	KD3 - Achievement of Stage 3 (1178 days)	0		20-May-17*	0												
KD002	KD2 - Achievement of Stage 2 (1232 days)	0		13-Jul-17*	0												
Possession Dates and Vacation Dates																	
PO-IVa2_b	Possession of Portion IVa (Day 930) - SR1	203	30-Mar-17 A	18-Oct-17	-369												
PO-Vb2_b	Possession of Portion V (Day 607) - SCP3	182	20-Apr-17	18-Oct-17	-343												
PO-IVc	Possession of Portion IVc (Day 1144) - MVB (above +5.0mPD)	111	30-Jun-17	18-Oct-17	-74												
Submissions and Approvals																	
Initial General Submission																	
1211	Submission of 1st Project video film	0		17-Apr-17 A													
9932	Submission of 1st Project video film Video1 / Video2 (Release II)	0		20-Apr-17*	-809												
DETAILED DESIGN OF WORKS																	
Permanent Works Design and Engineering																	
Metal Roof on MVB																	
2188	MVB Roof - Engineer review & approval	24	06-Mar-17 A	05-May-17	-259												
2190	MVB Roof - Prepare the Detailed Design submission	12	06-May-17	19-May-17	-259												
2192	MVB Roof - Finalise detailed design submission and ICE Checks & issue Check Certificate	12	20-May-17	03-Jun-17	-259												
12436	MVB Roof - Submit detailed design to the Engineer with ICE Certificate	0		03-Jun-17	-259												
2194	MVB Roof - Engineer review & Approval; Consent to Proceed Construction	24	05-Jun-17	03-Jul-17	-257												
Green Roof on EVB																	
2166	EVB Roof - Engineer review & Approval; Consent to Proceed Construction	24	18-Apr-16 A	05-May-17	-324												



**Leighton Contractors (Asia) Limited
Programme Update 38 (April 2017)
THREE MONTH ROLLING**

Project ID: H2613-U038
Baseline: DWP2d
Layout: Update Three Month Rolling
U038
Page 1 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

Data Date: 20-Apr-17		CWB(CC) - Commissioning Contract TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017												
						Apr			May			Jun			Jul			
Green Wall on ADB																		
10238	ADB Green Wall - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	05-May-17	-304													
Landscaping & Associated Irrigation System																		
10268	Landscaping - Engineer review & Approval; Consent to Proceed Construction	24	07-Mar-16 A	05-May-17	-103													
Building Services System																		
MVAC System																		
ITP, Method Statement & Testing & Commissioning Plan																		
11070	MVAC System - Testing & Commissioning submission Plan to AECOM	70	22-Jan-16 A	05-May-17	-159													
Plumbing System (PL)																		
ITP, Method Statement & Testing & Commissioning Plan																		
11112	PL System - Testing & Commissioning Plan submission to AECOM (review / approval)	90	16-Oct-15 A	27-Mar-17 A														
Drainage System (DR)																		
ITP, Method Statement & Testing & Commissioning Plan																		
11126	DR System - Testing & Commissioning Plan to AECOM	90	14-Nov-15 A	06-Apr-17 A														
Access Road at Area D & E																		
12720	Access Road atArea D & E - Prepare design submission	24	28-Apr-17*	27-May-17	-89													
12726	Access Road atArea D & E - Submission of design to MTRC / AECOM	0		27-May-17	-89													
12724	Access Road atArea D & E - MTRC/AECOM review & Approval; Consent to Proceed Construction	28	29-May-17	30-Jun-17	-89													
PROCUREMENT, MANUFACTURING & DELIVERIES																		
Procurement; Manufacturing; Deliveries																		
Metal Roof on MVB																		
Shop Drawings																		
2200	MVB Roof - Shop Drawings submission to the Engineer	30	05-May-17	03-Jun-17	-324													
12842	MVB Roof - Shop Drawings review by the Engineer	30	04-Jun-17	03-Jul-17	-324													

◆

Current Milestone

Level of Effort

▲

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING


Project ID: H2613-U038

Baseline: DWP2d

Layout: Update Three Month Rolling U038

Page 2 of 40

Date	Revision	Checked	Appro..
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

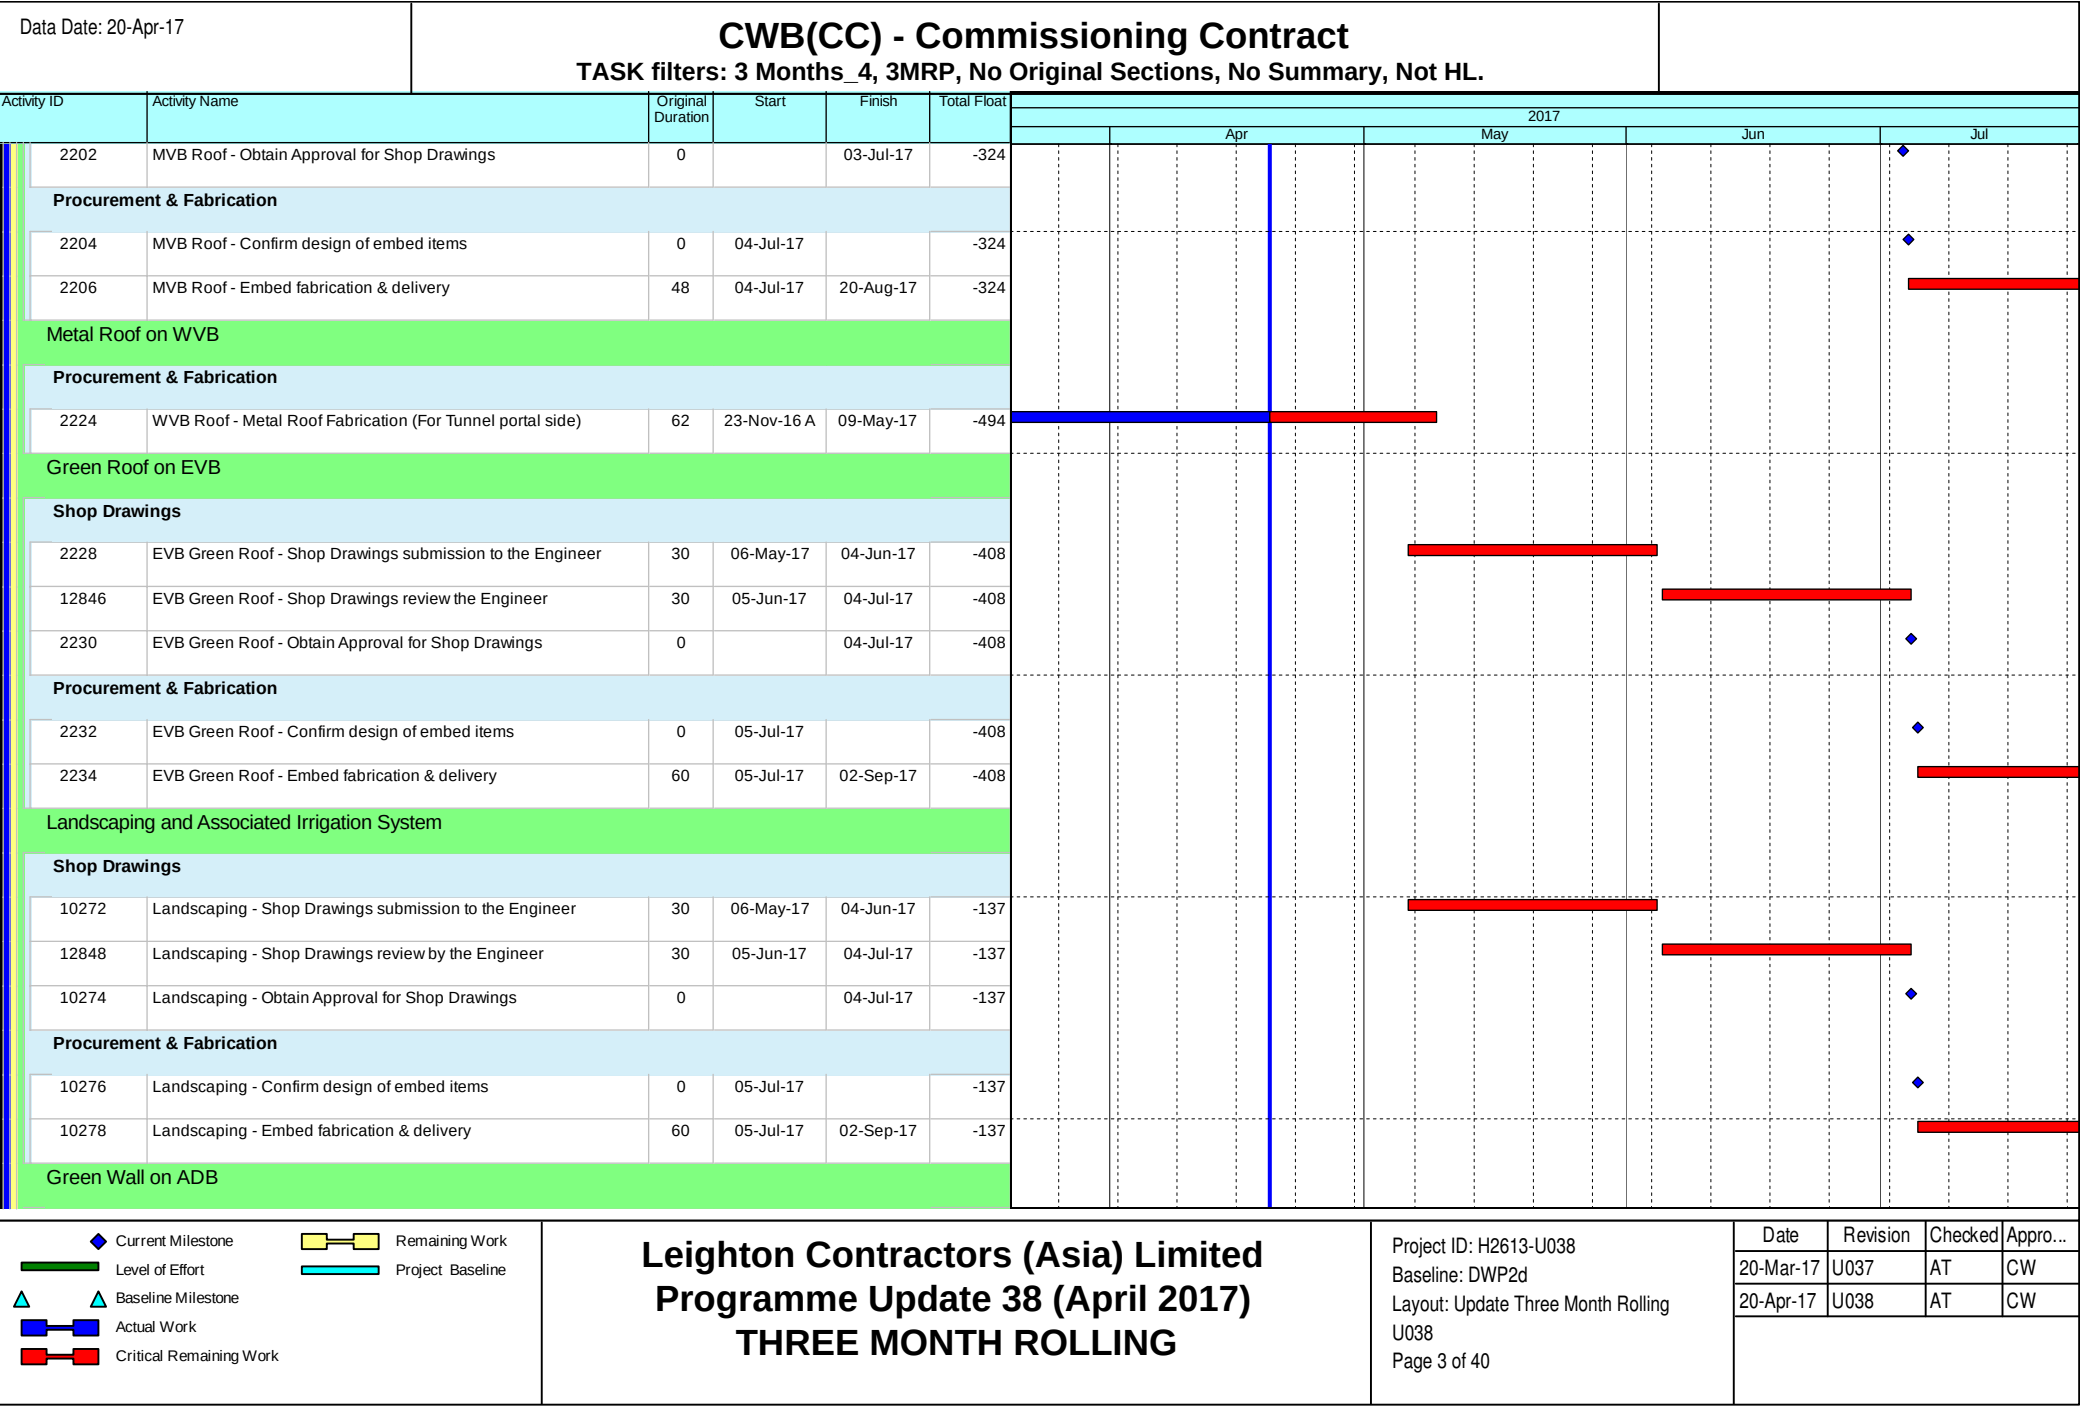


Data Date: 20-Apr-17

CWB(CC) - Commissioning Contract

TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017											
						Apr			May			Jun			Jul		
Shop Drawings																	
10242	ADB Green Wall - Shop Drawings submission to the Engineer	30	06-May-17	04-Jun-17	-380												
12850	ADB Green Wall - Shop Drawings review the Engineer	30	05-Jun-17	04-Jul-17	-380												
10244	ADB Green Wall - Obtain Approval for Shop Drawings	0		04-Jul-17	-380												
Procurement & Fabrication																	
10246	ADB Green Wall - Confirm design of embed items	0	05-Jul-17		-380												
10248	ADB Green Wall - Embed fabrication & delivery	60	05-Jul-17	02-Sep-17	-380												
VE Brackets / Panels																	
Procurement & Fabrication																	
12508	VE Brackets / Panels - Manufacturing & Delivery (Panels)	60	11-Dec-15 A	09-May-17	-192												
Architectural Feature on EVS																	
Procurement & Fabrication																	
10086	EVS - Architectural Features delivery	60	09-Jun-17	07-Aug-17	-452												
2254	EVS - Commence installation	0	09-Jul-17		-452												
Air Purification System (APS)																	
Procurement & Fabrication																	
10088	APS - Ship to HK Store (2nd Batch)	80	18-Jan-17 A	16-Jun-17	-175												
13664	APS - Ship to HK Store (3rd Batch)	80	19-Jun-17	06-Oct-17	-175												
Building Services System																	
Shop Drawings / CSD / CBWD																	
2314	BS(MVB) - Obtain Approval for Shop Drawings, CSD & CBWD	0		20-Apr-17	149												
2318	BS(EVB) - Obtain Approval for Shop Drawings, CSD & CBWD	0		20-Apr-17	105												
Thermal Barriers																	
Procurement & Fabrication																	




Leighton Contractors (Asia) Limited Programme Update 38 (April 2017) THREE MONTH ROLLING

Project ID: H2613-U038
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U038
 Page 4 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW


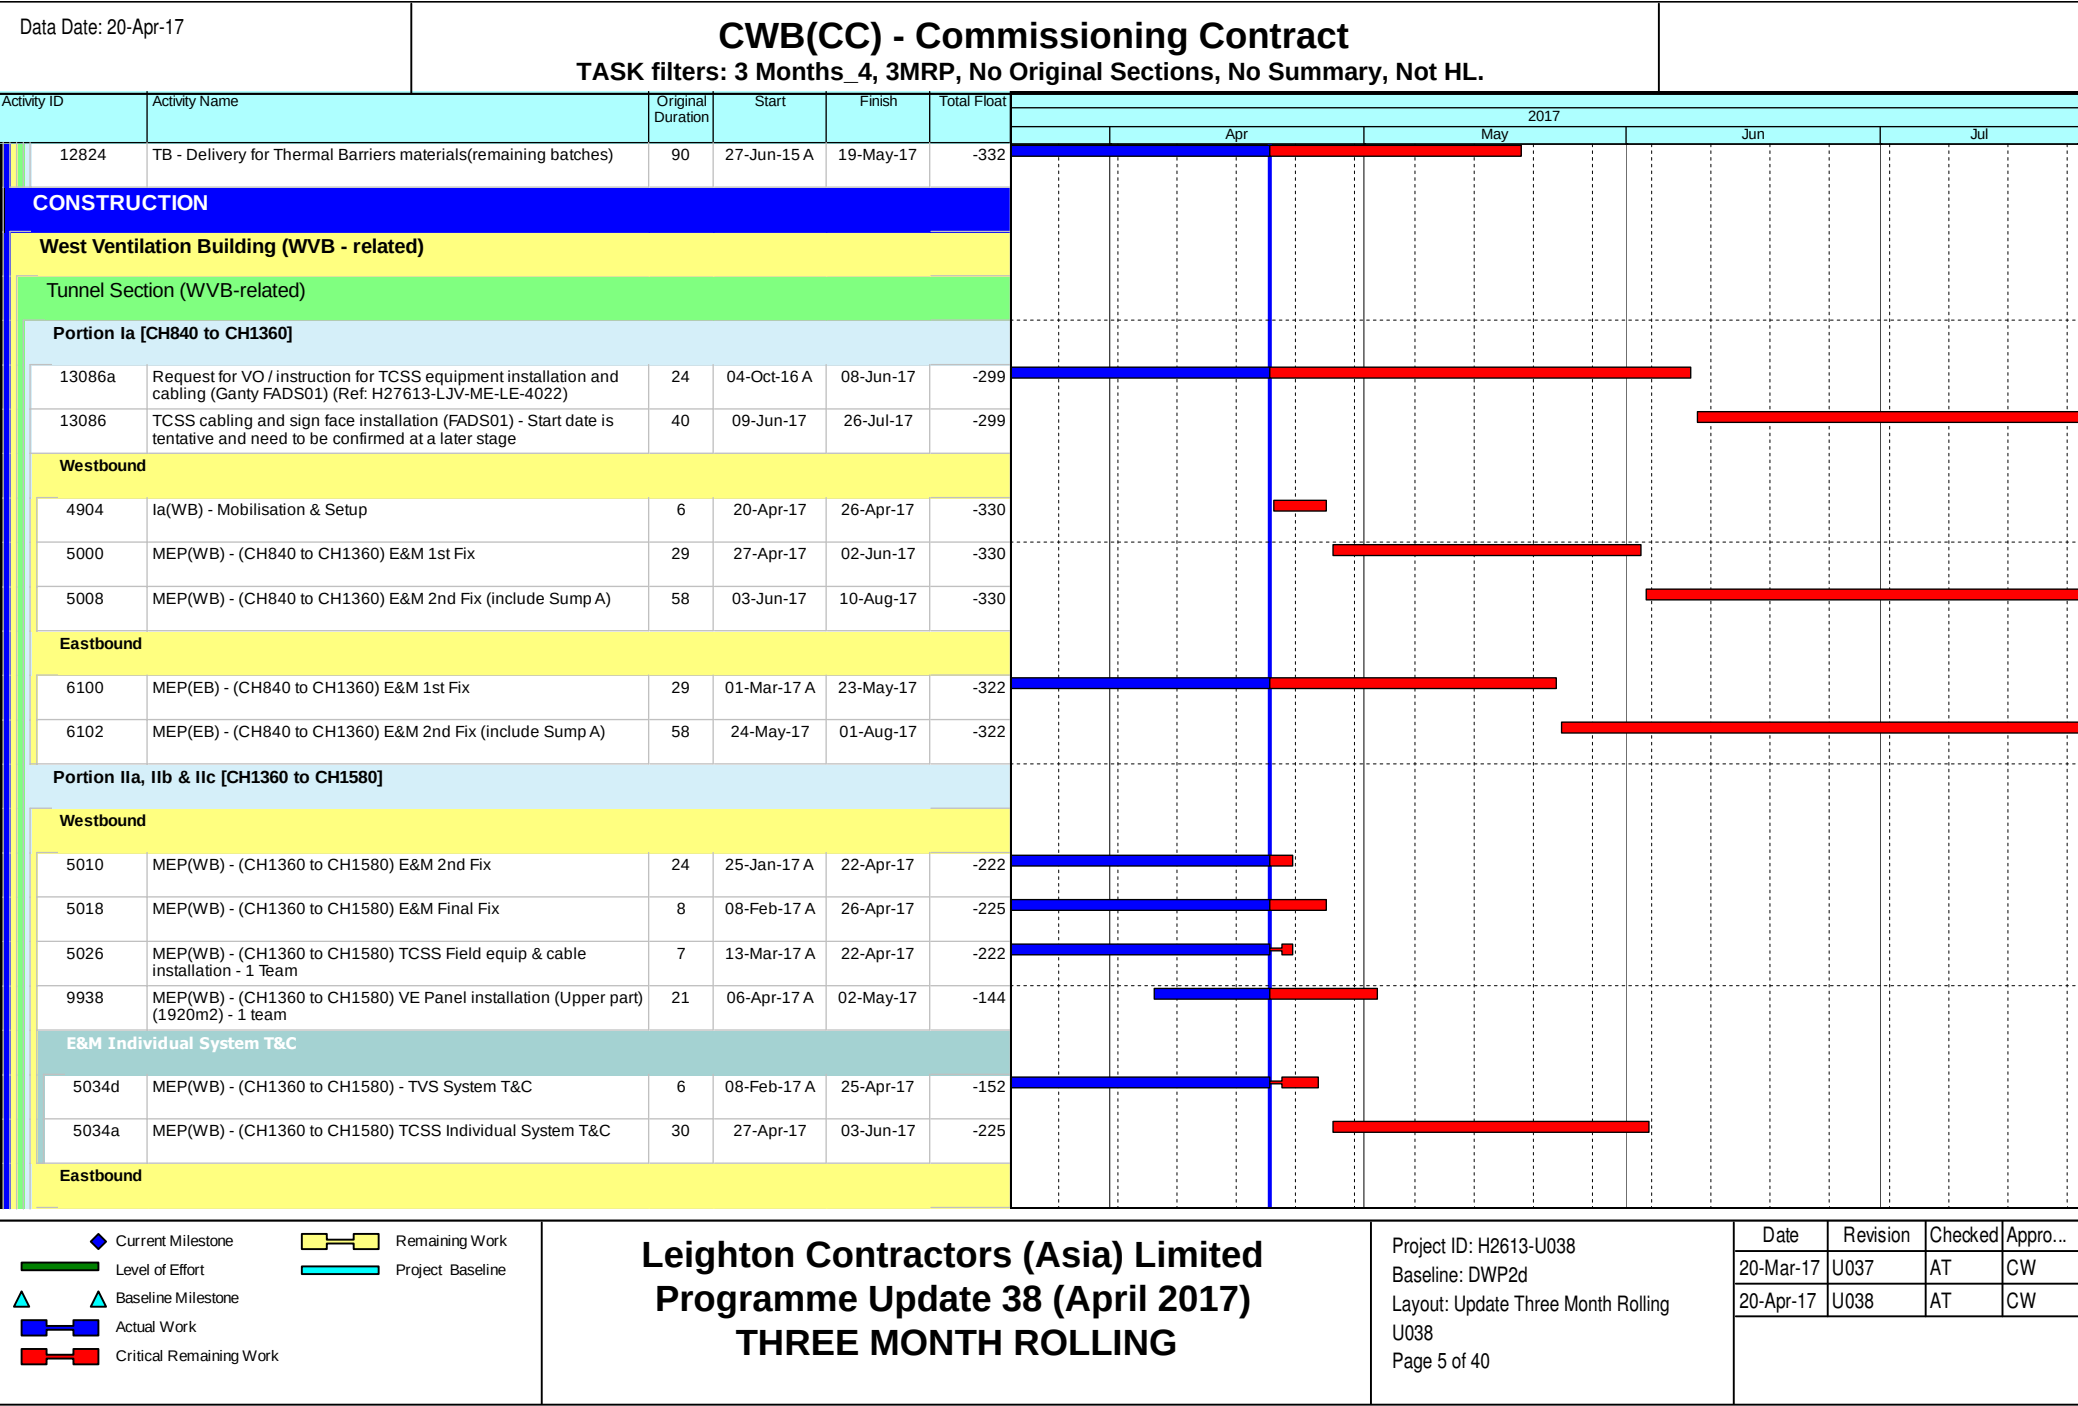


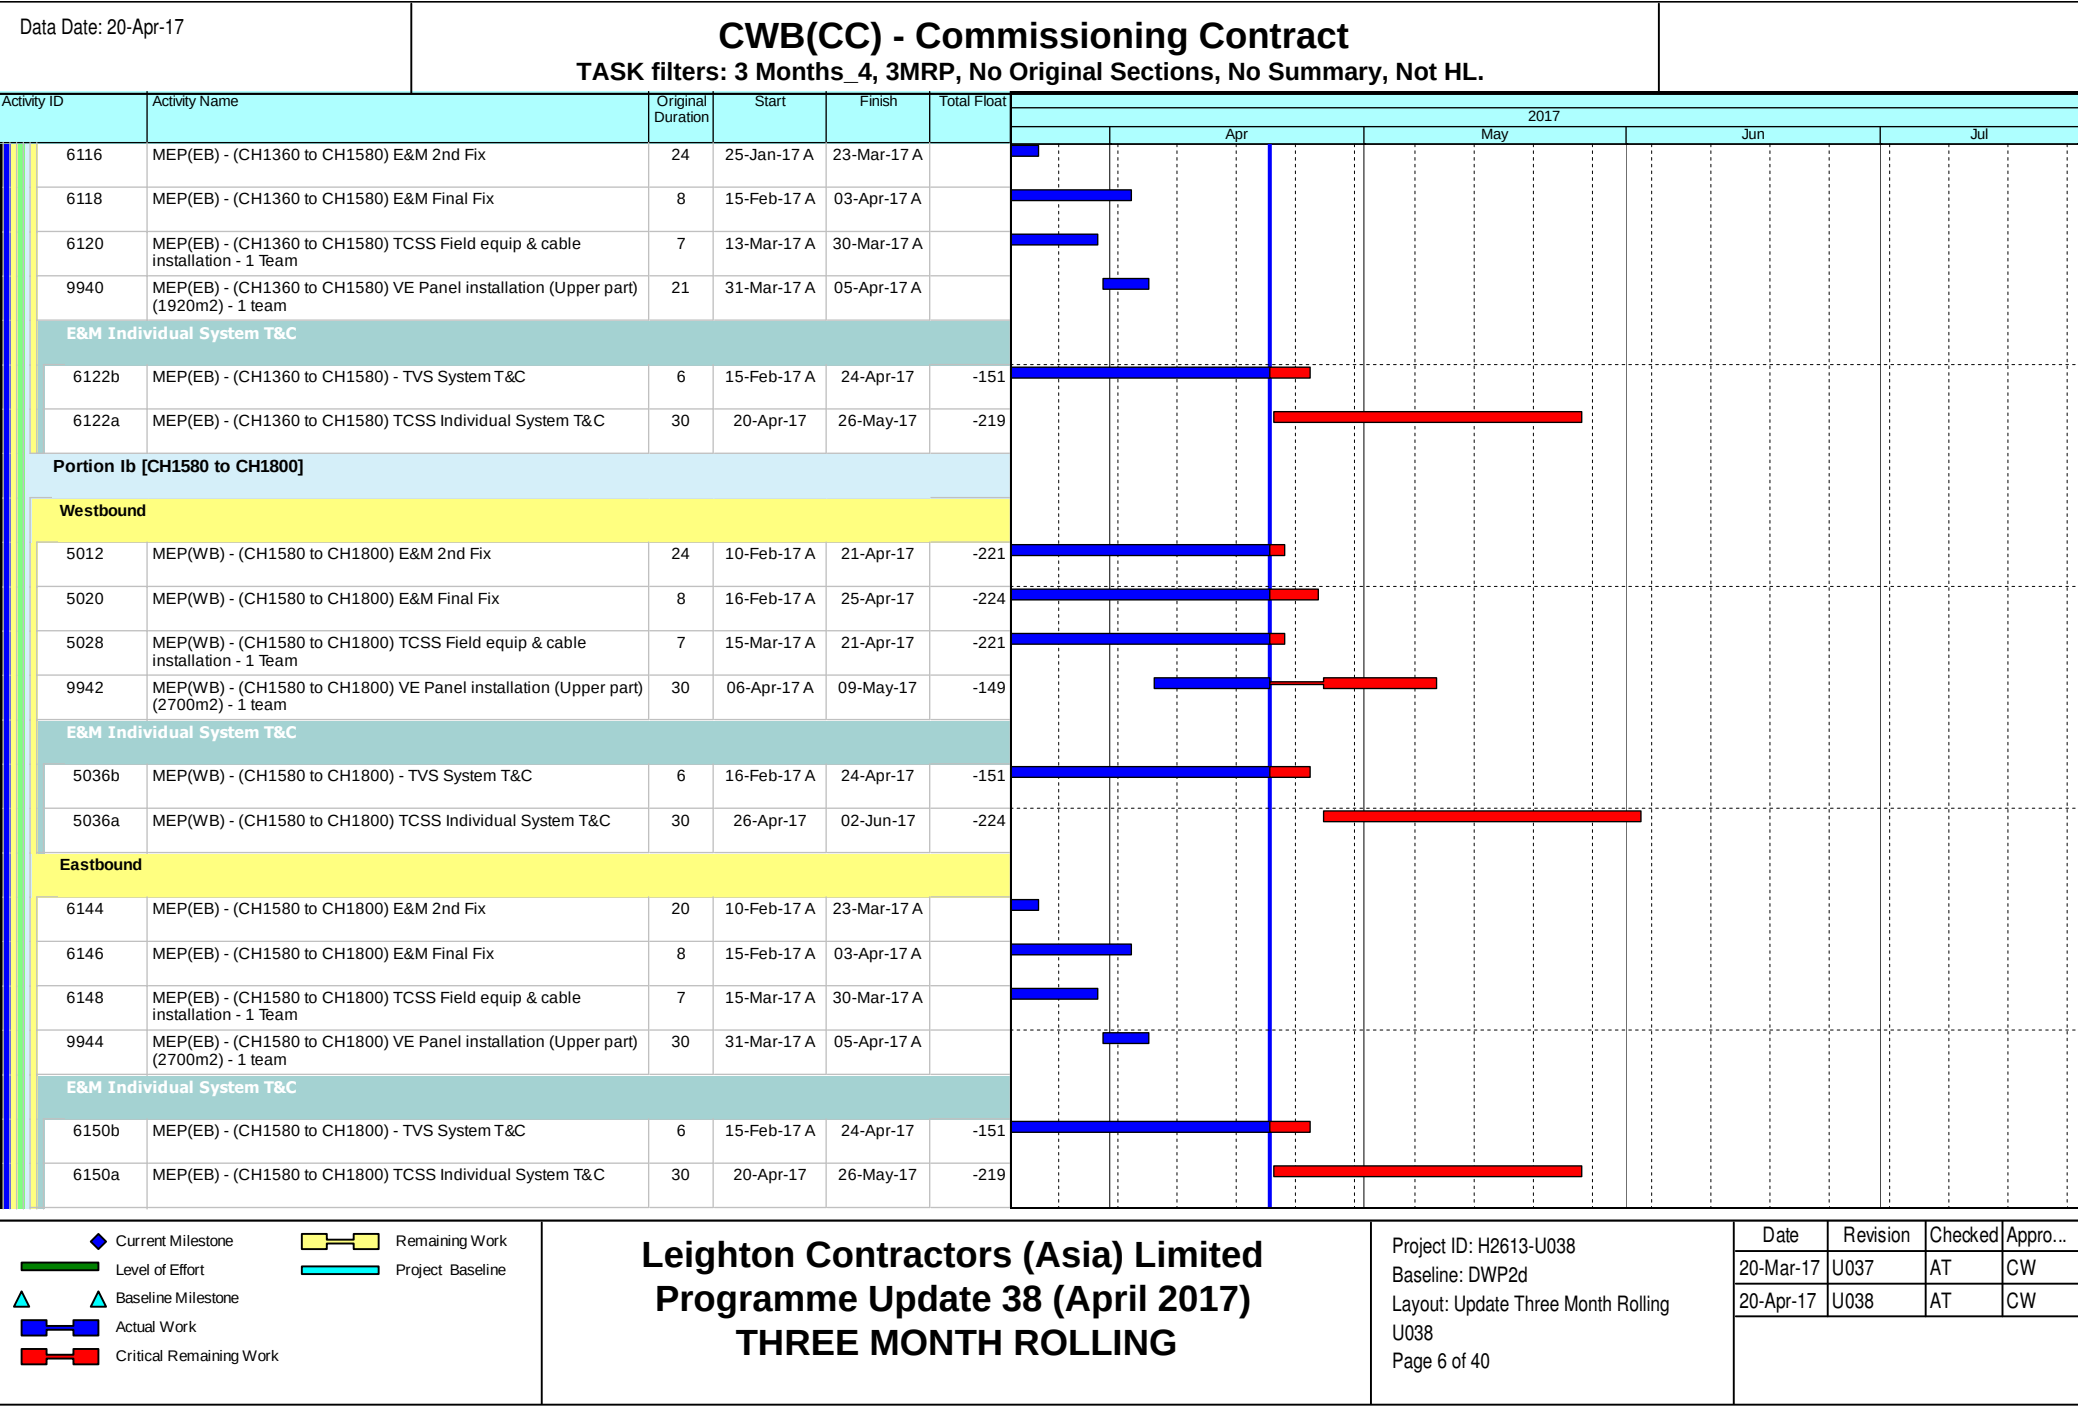

Data Date: 20-Apr-17

CWB(CC) - Commissioning Contract

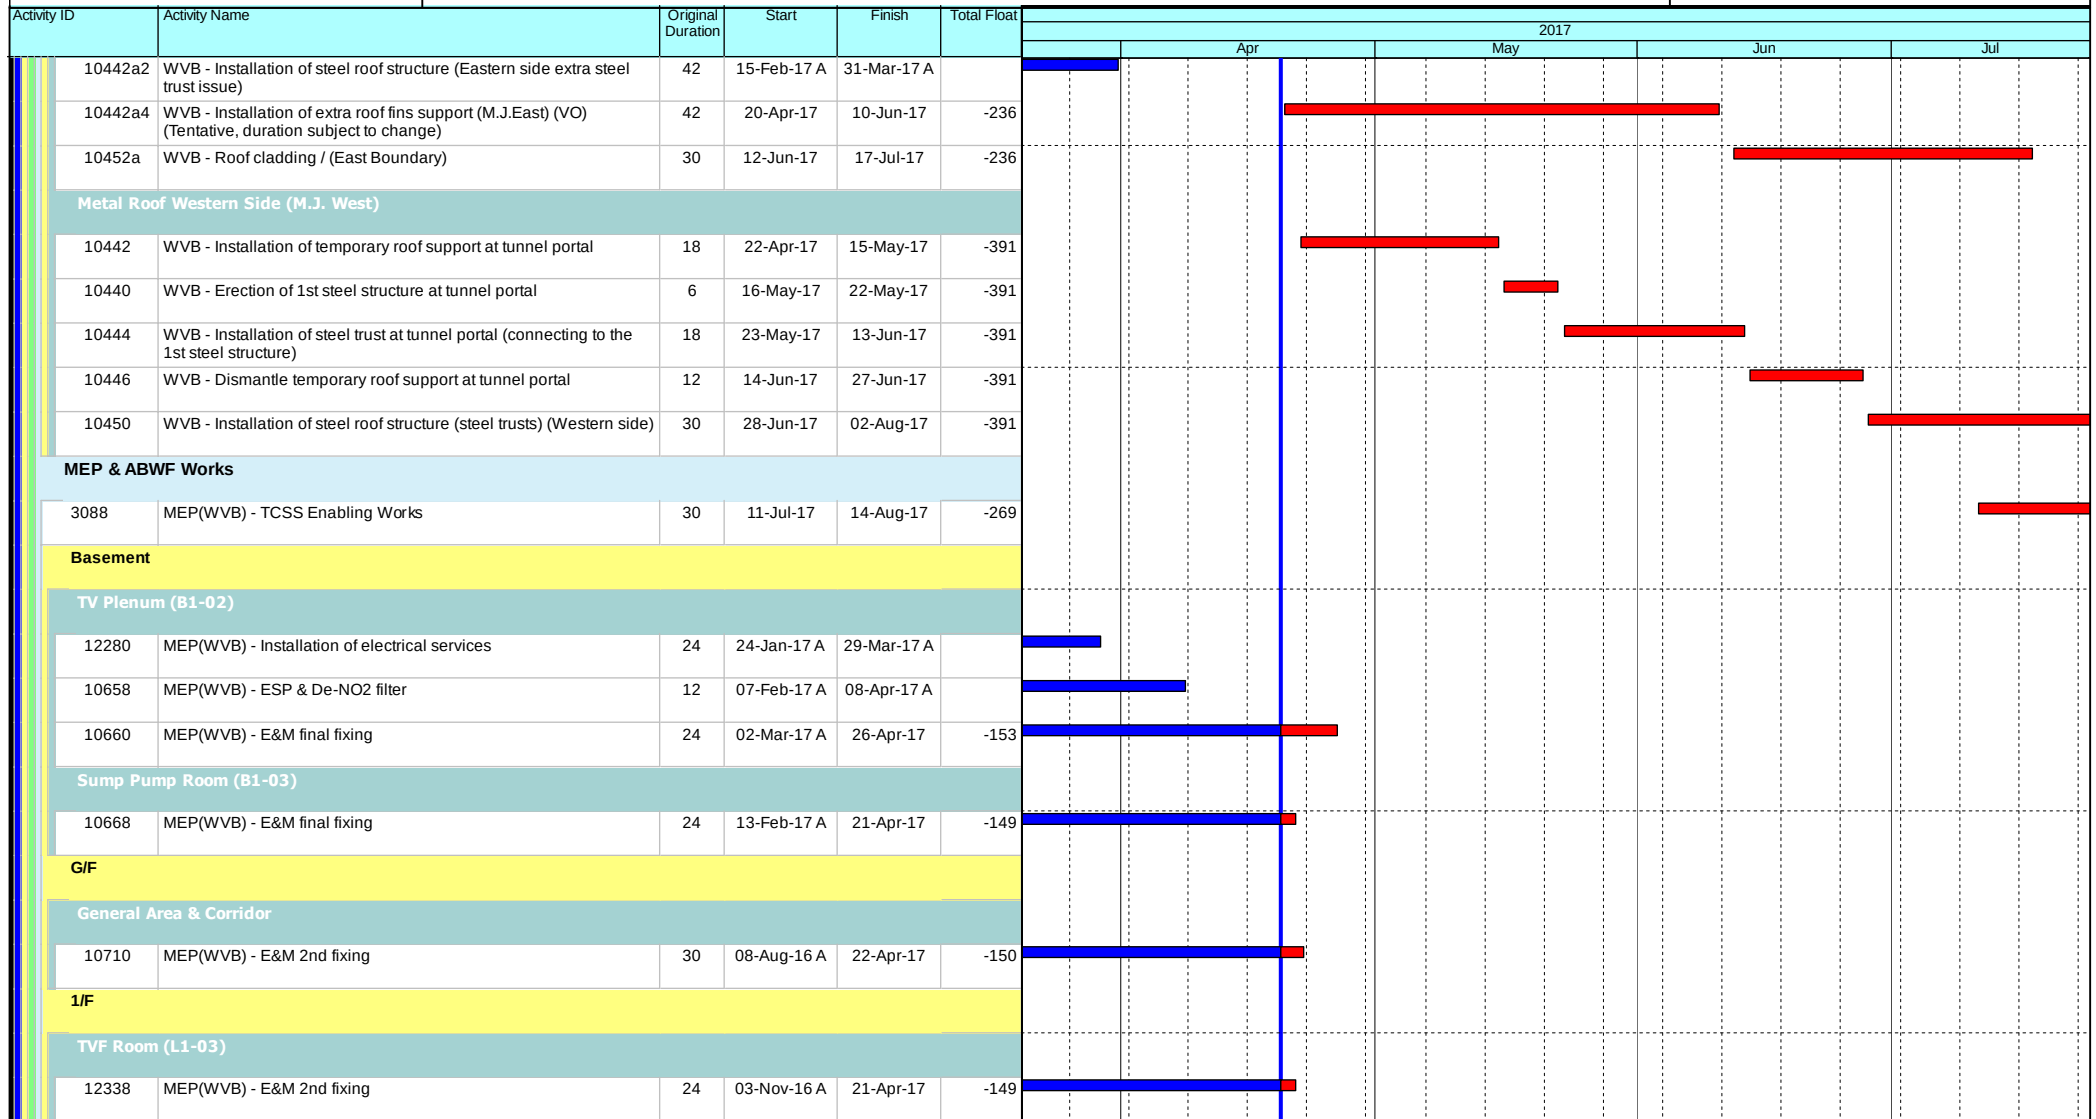
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.





Leighton Contractors (Asia) Limited Programme Update 38 (April 2017) THREE MONTH ROLLING


Project ID: H2613-U038
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U038
 Page 8 of 40


Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

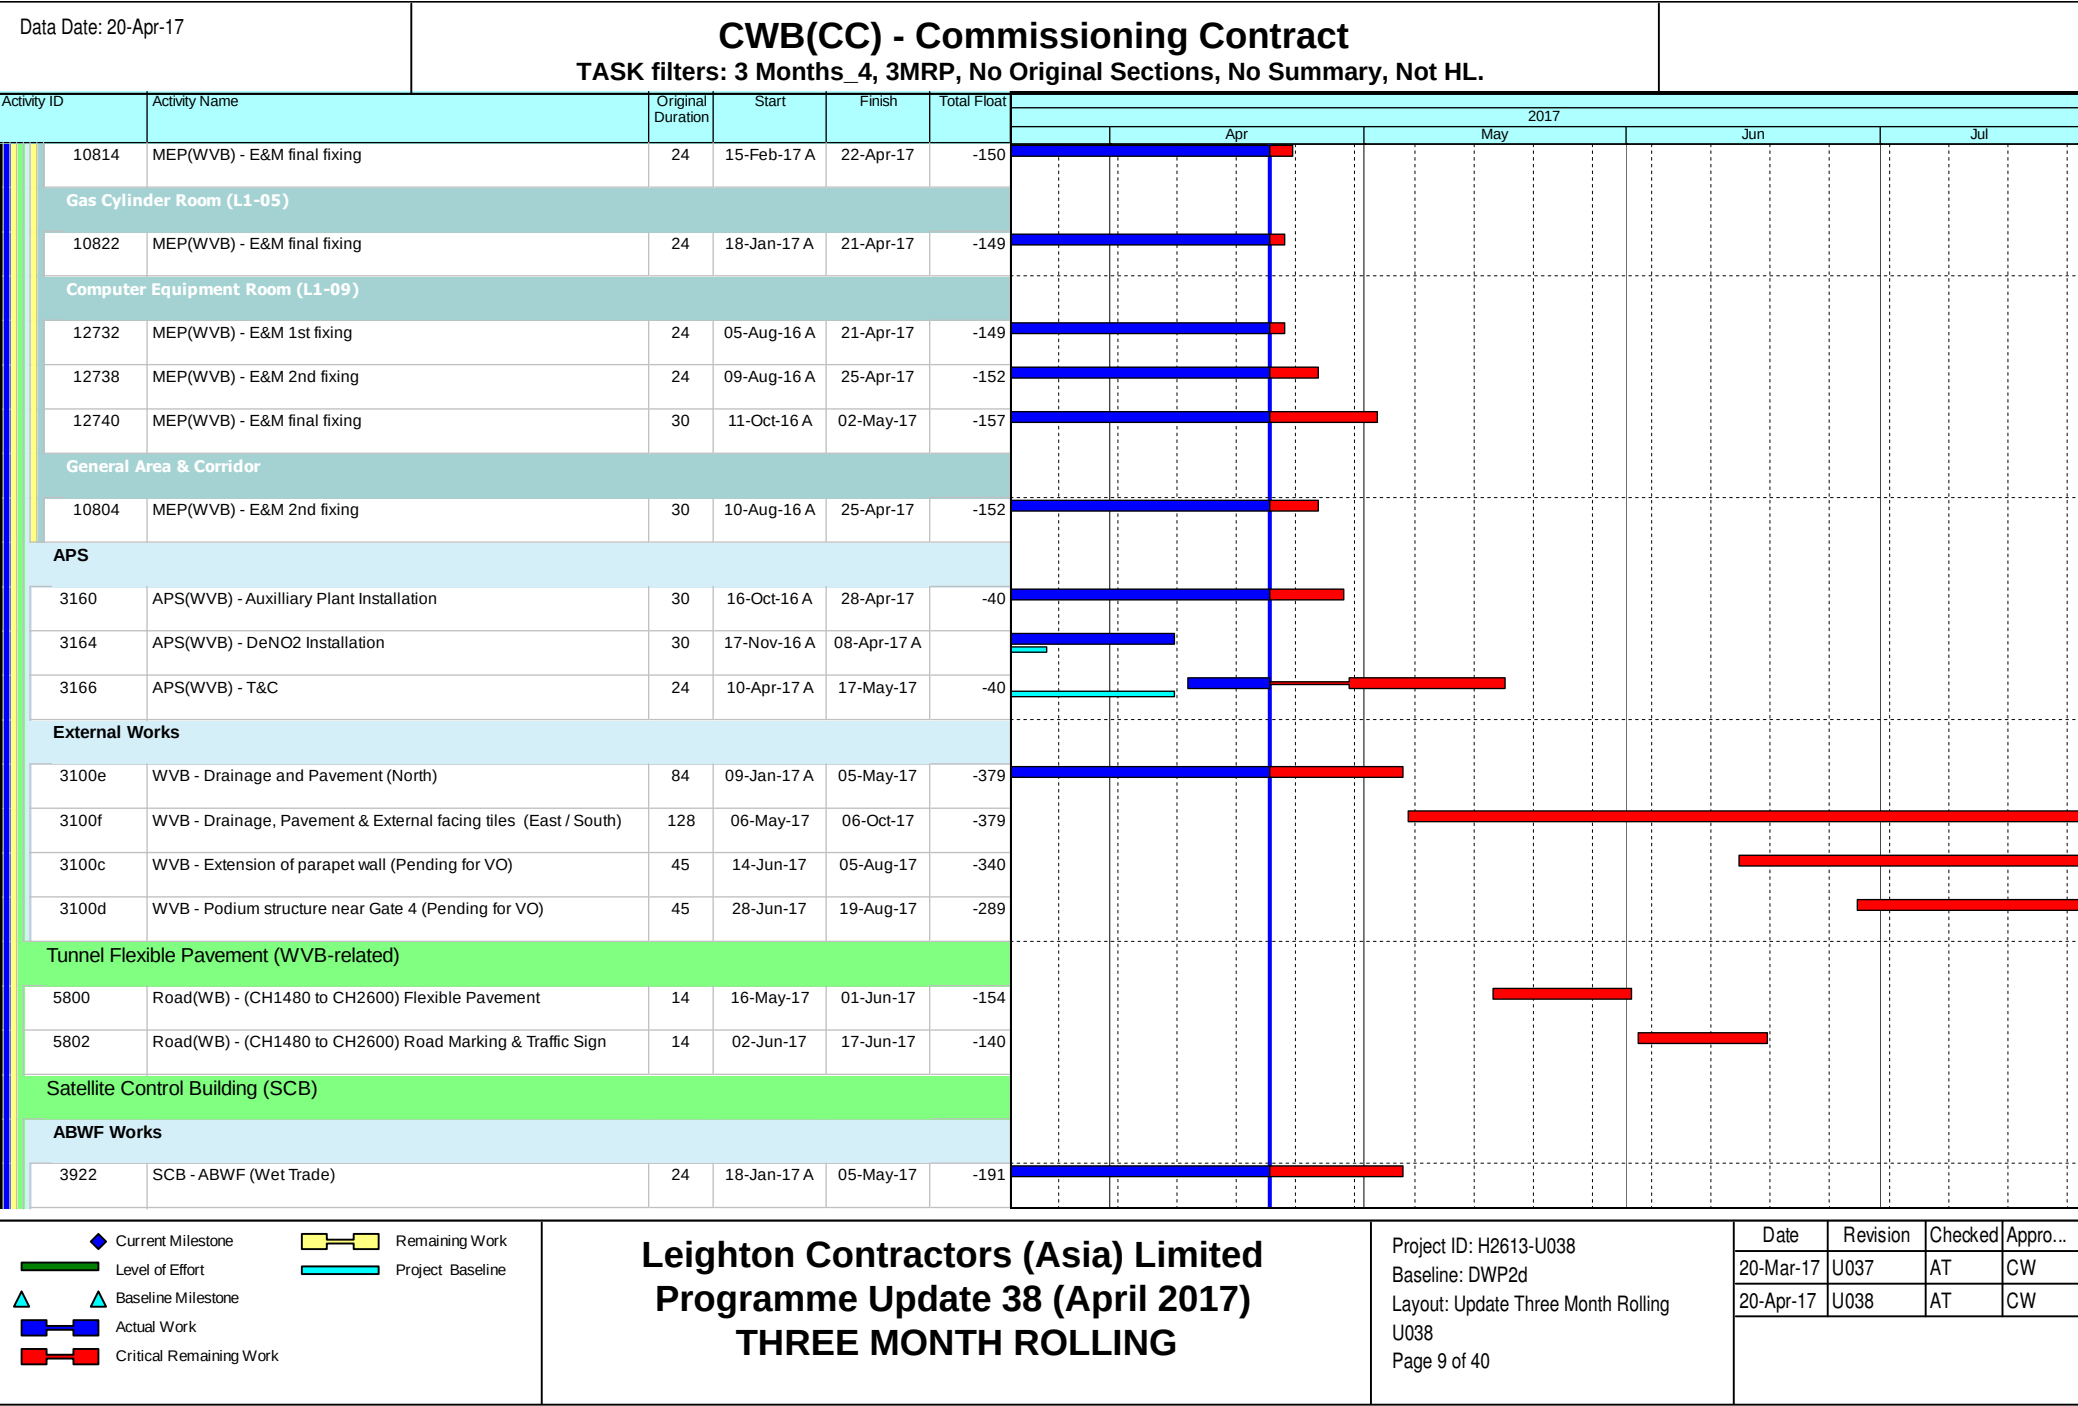


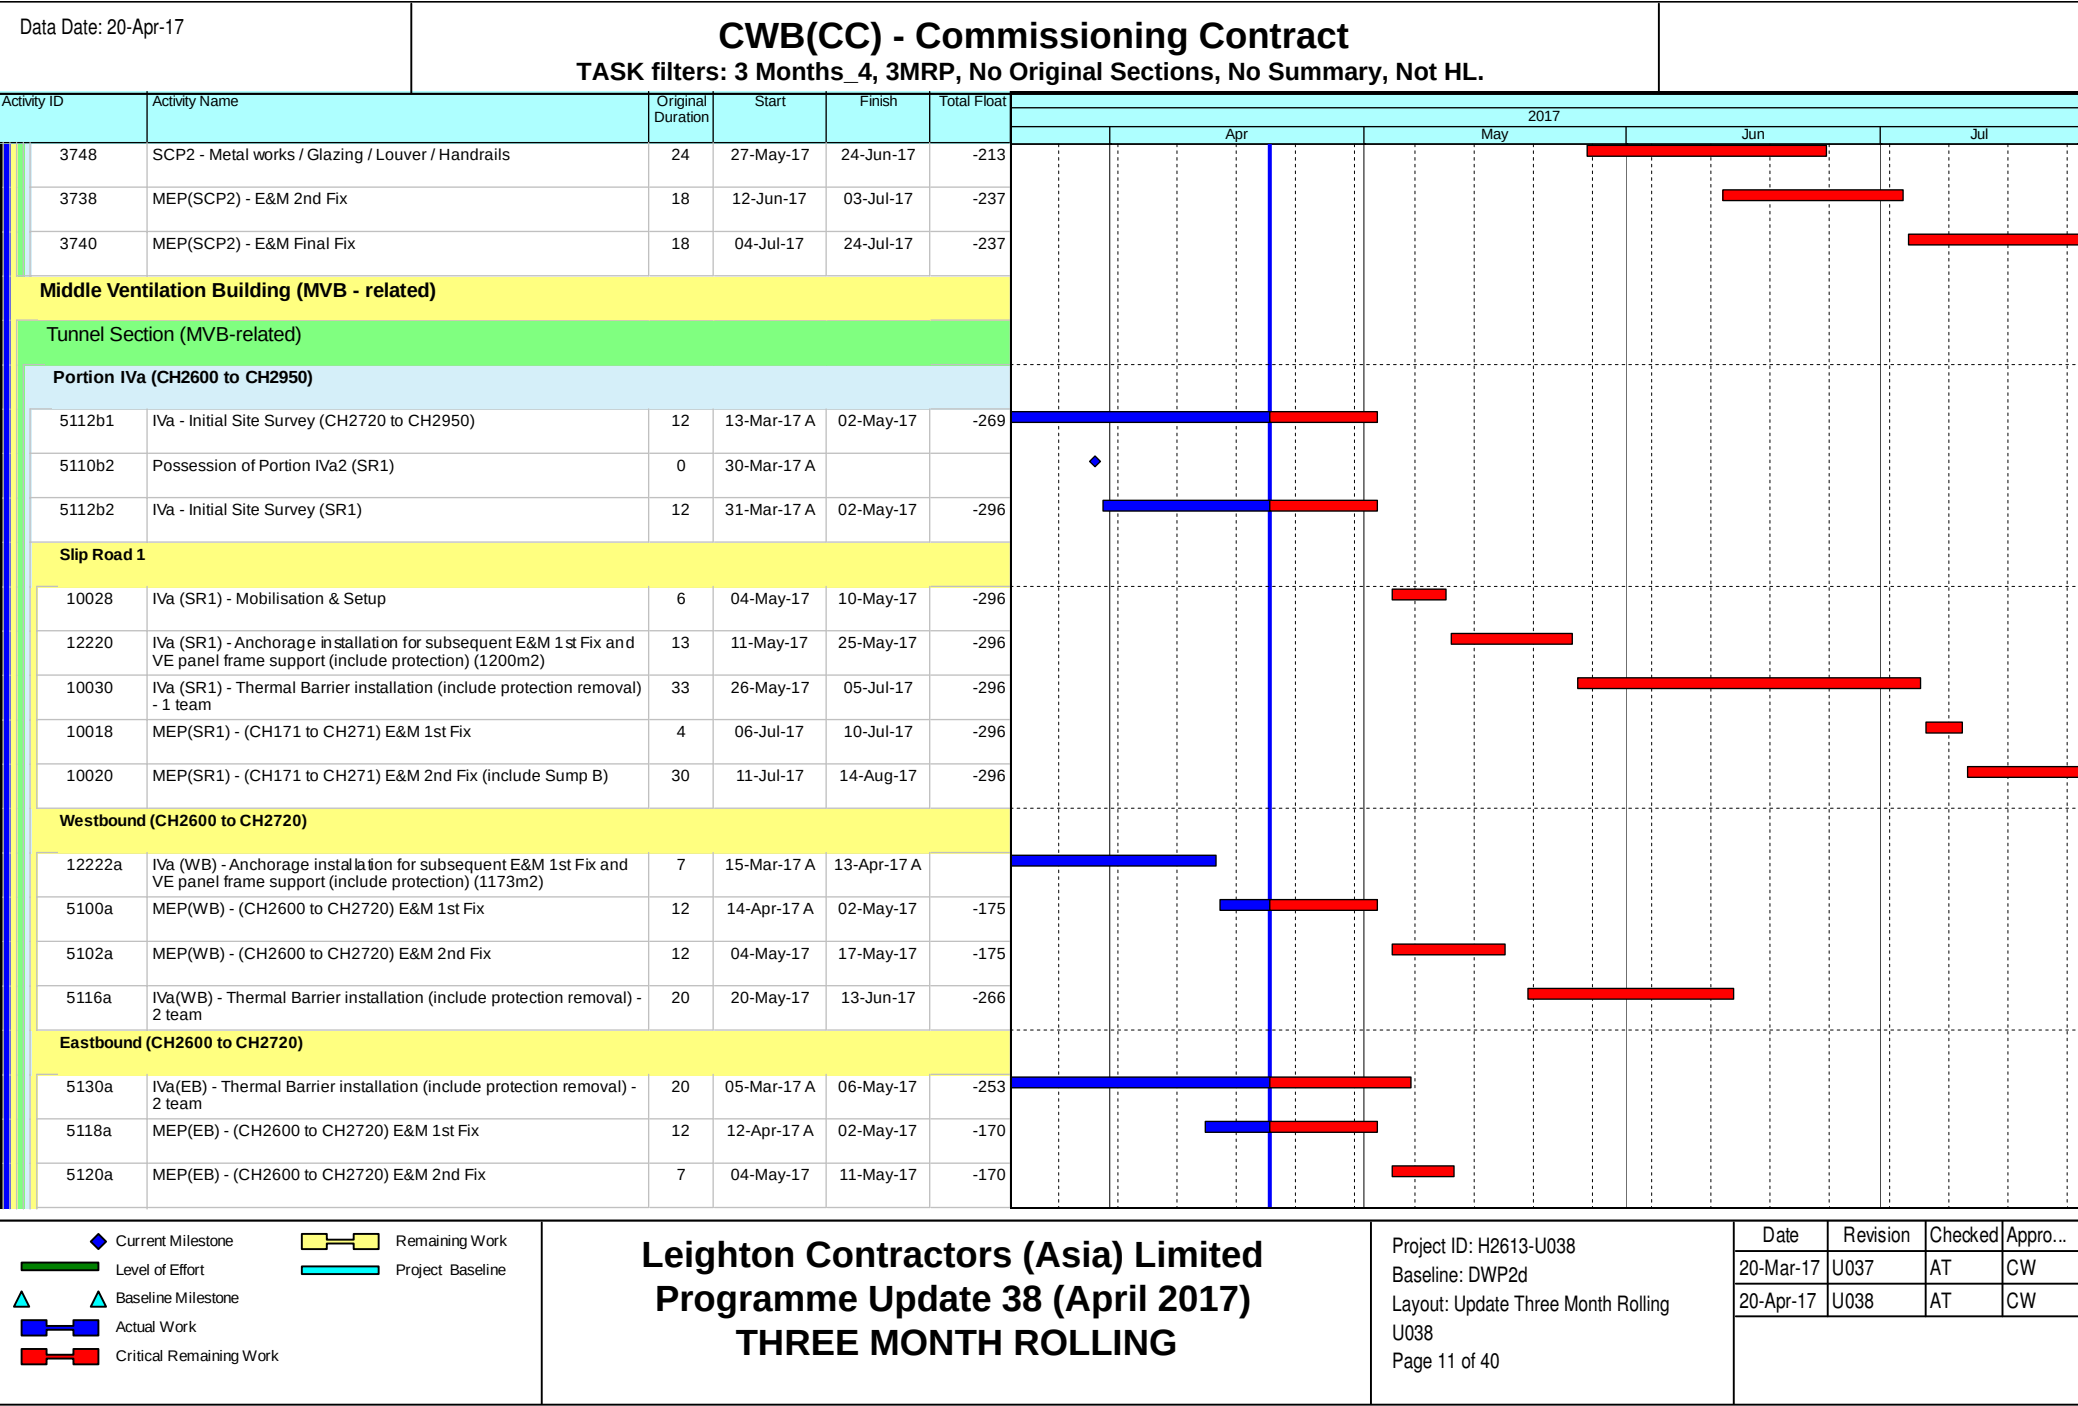


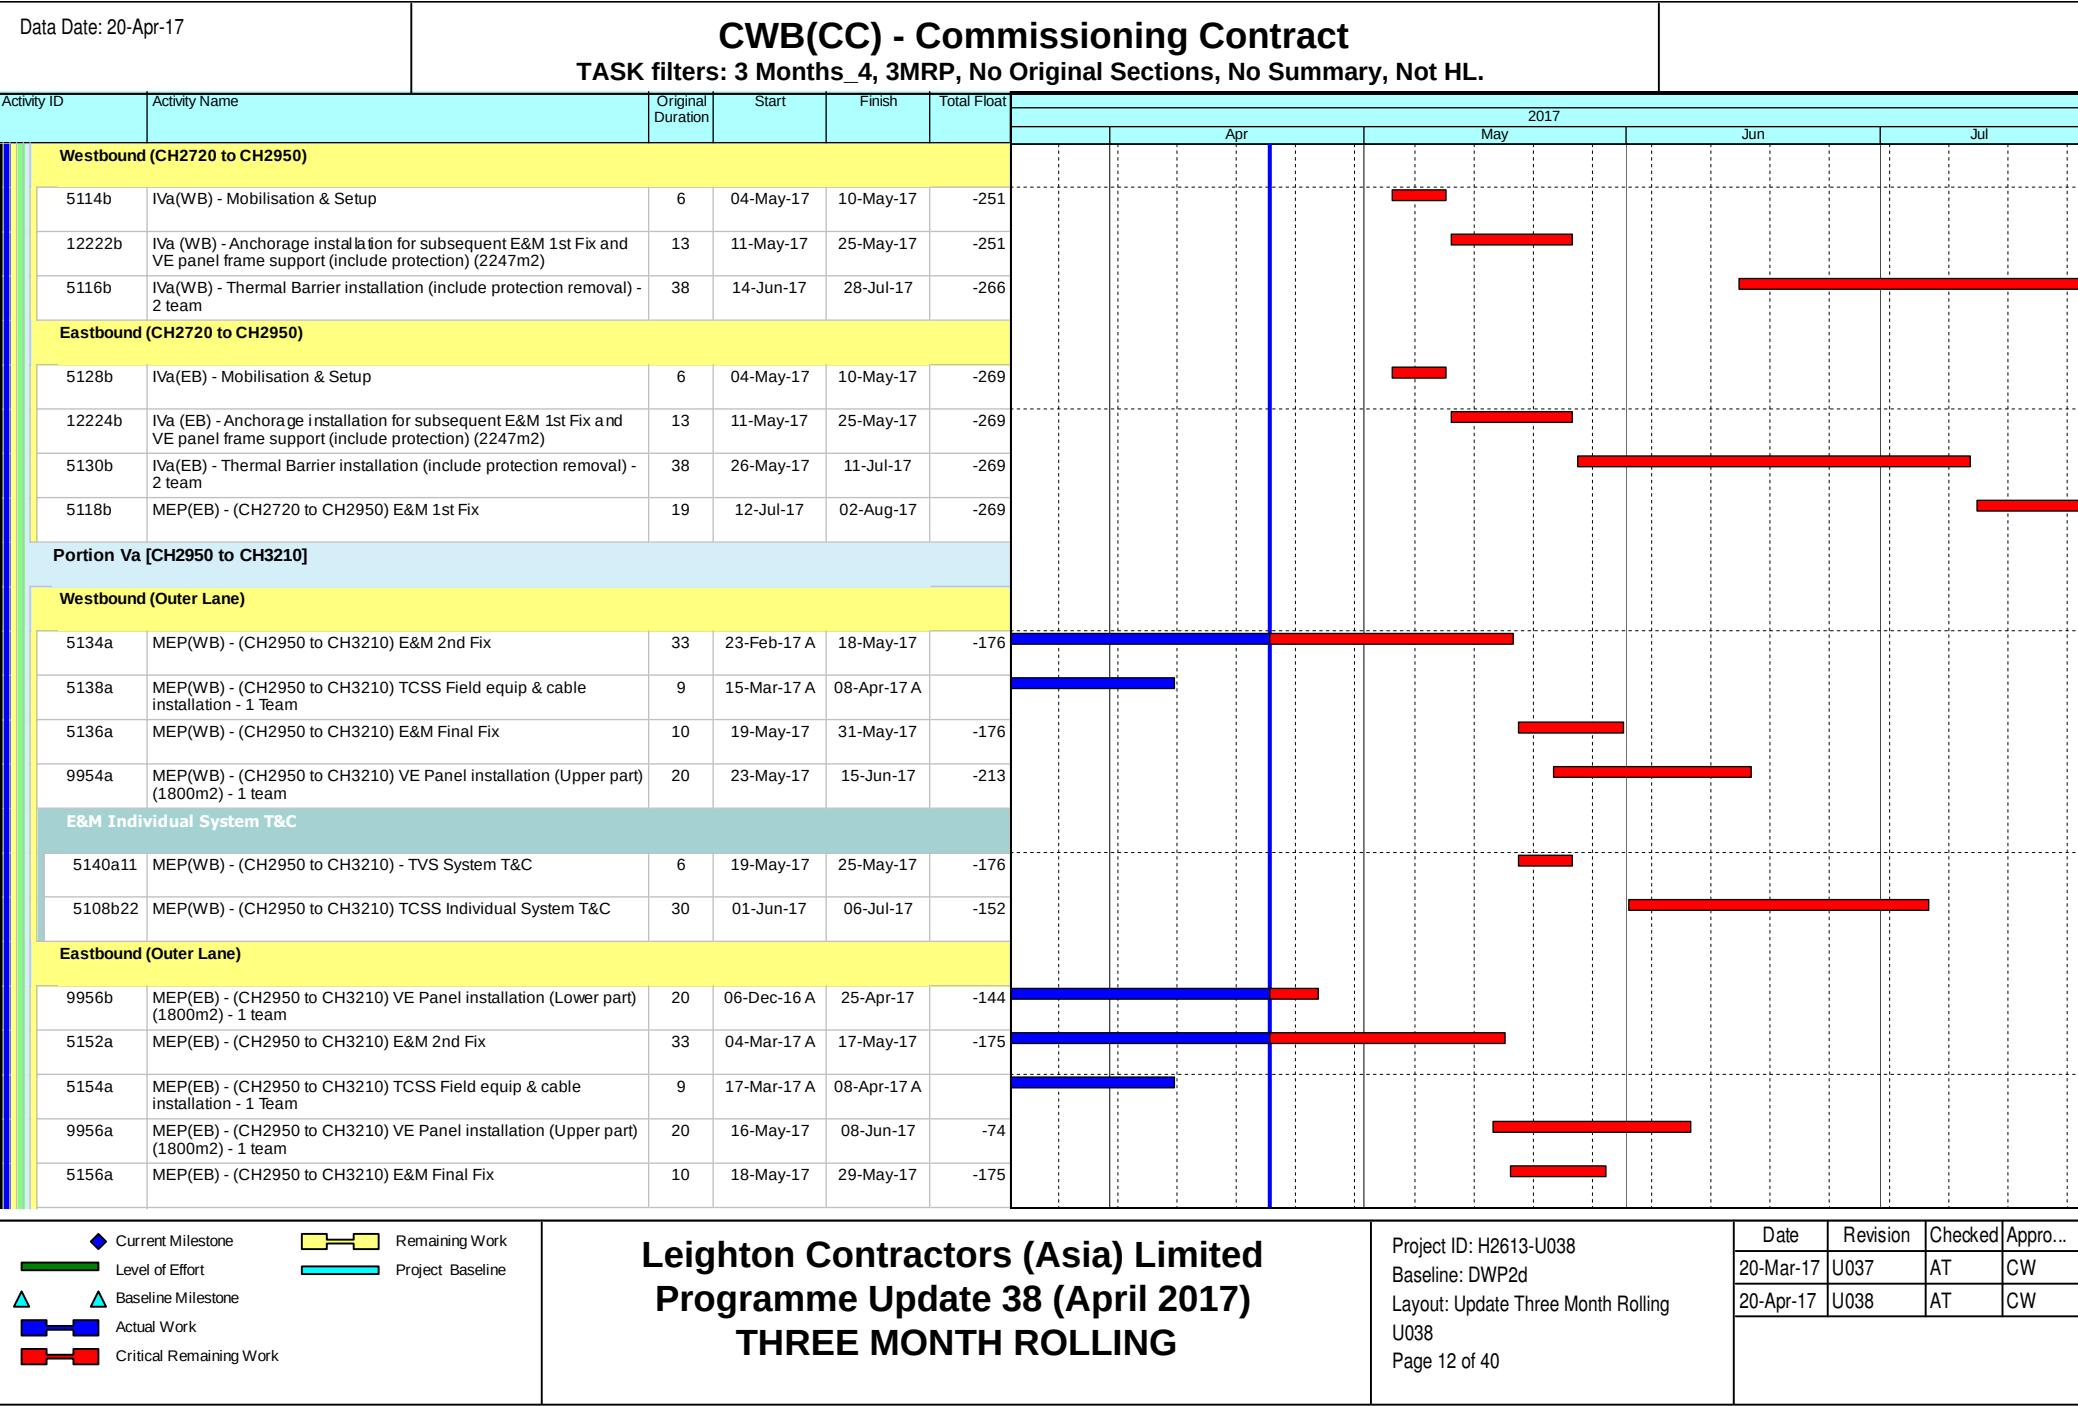


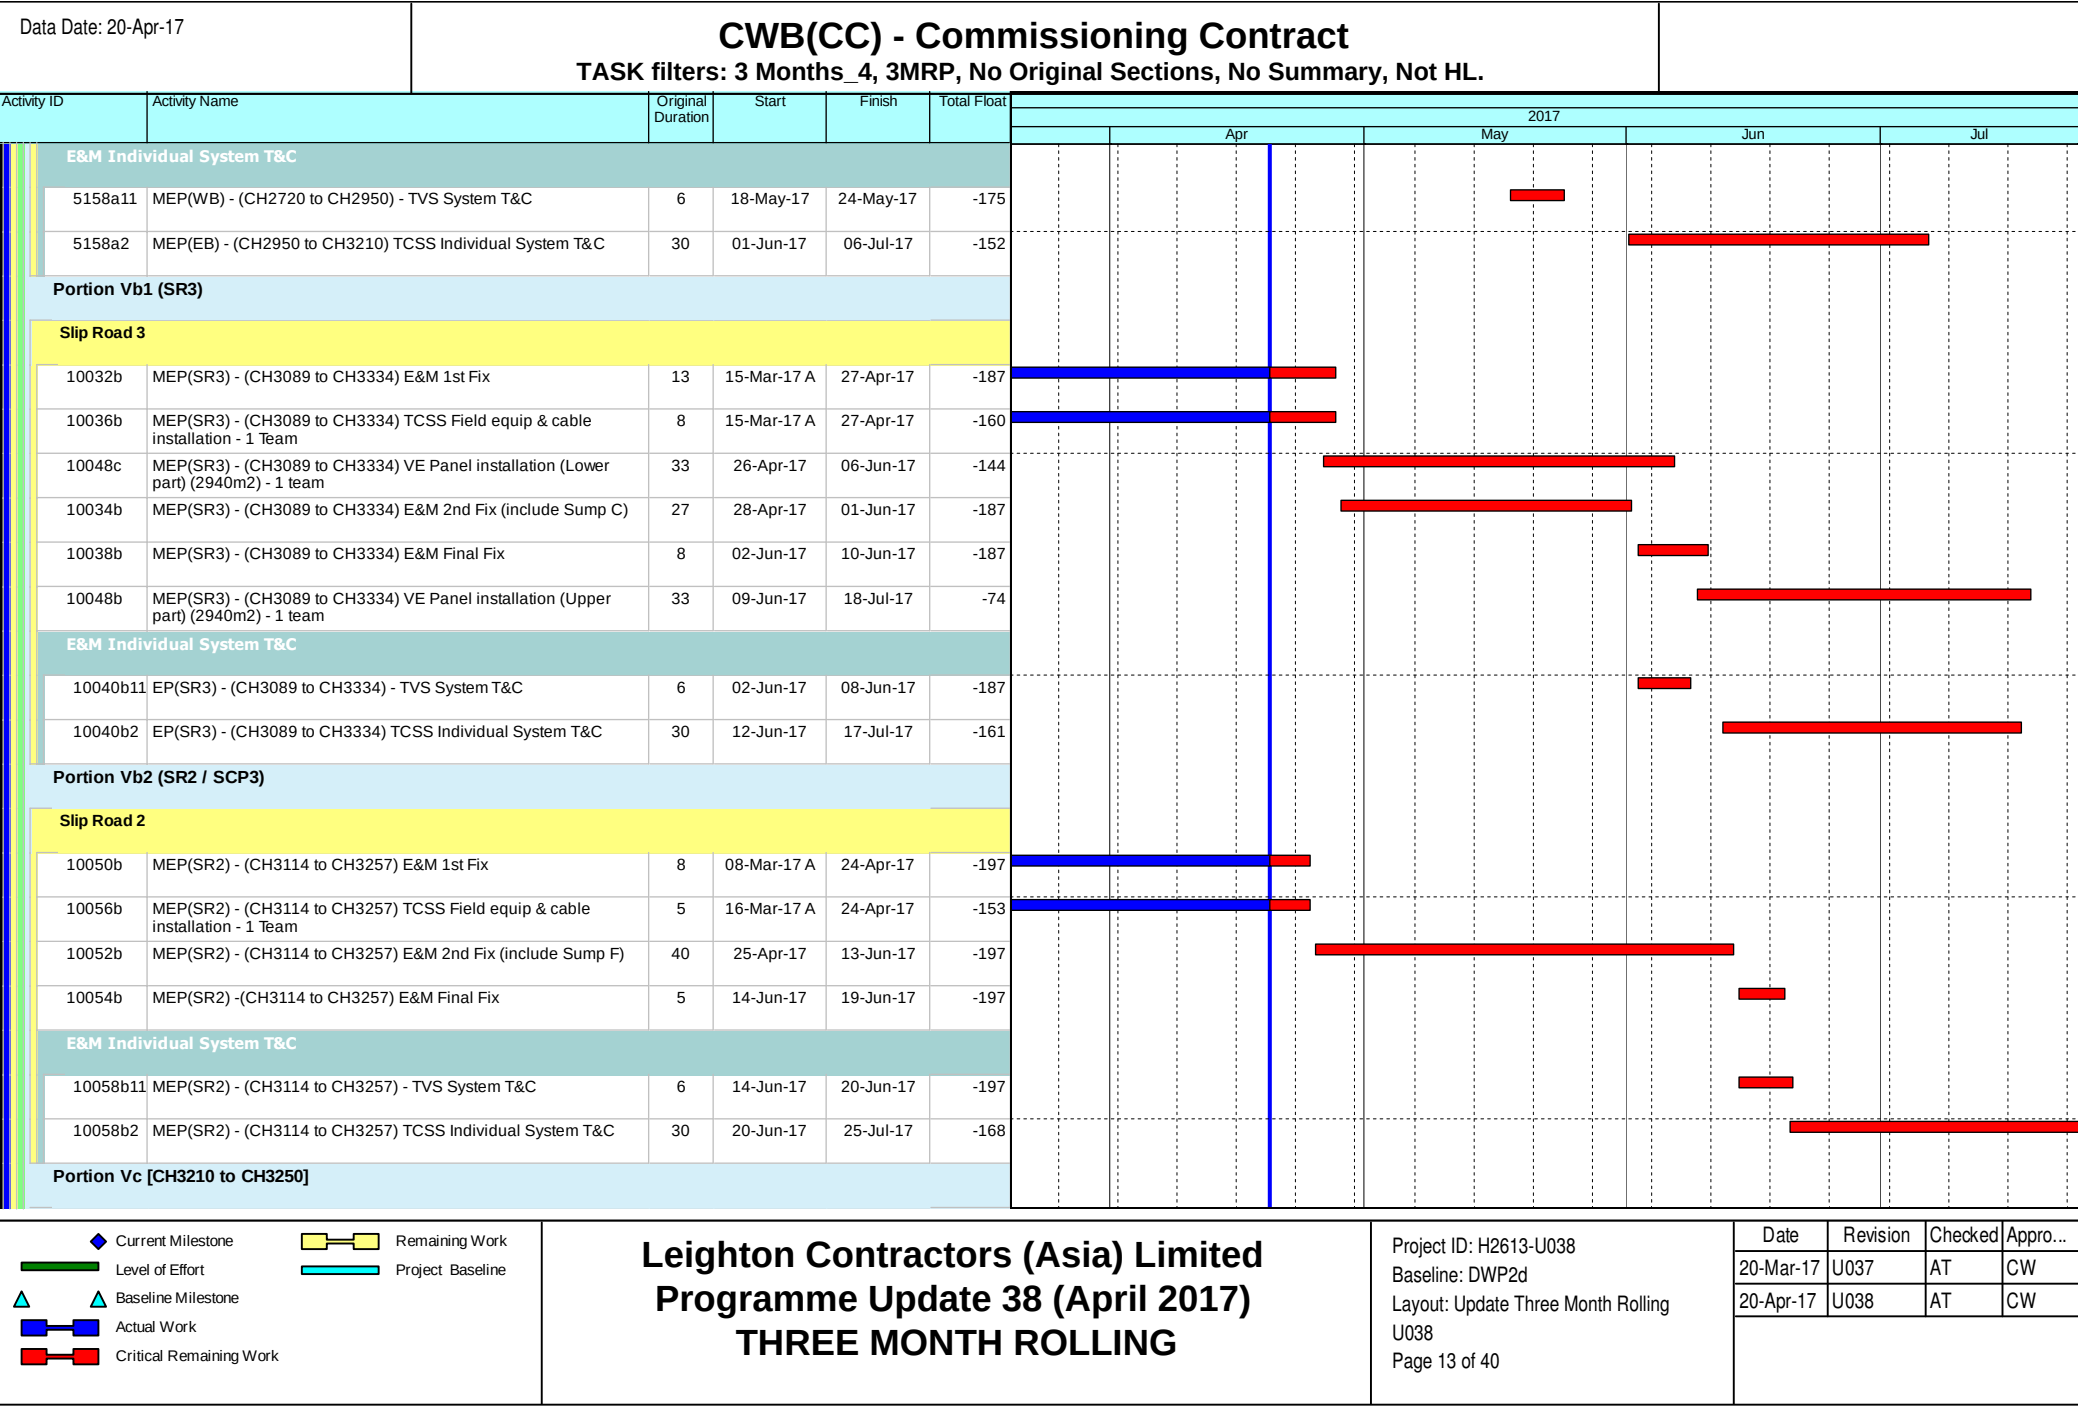

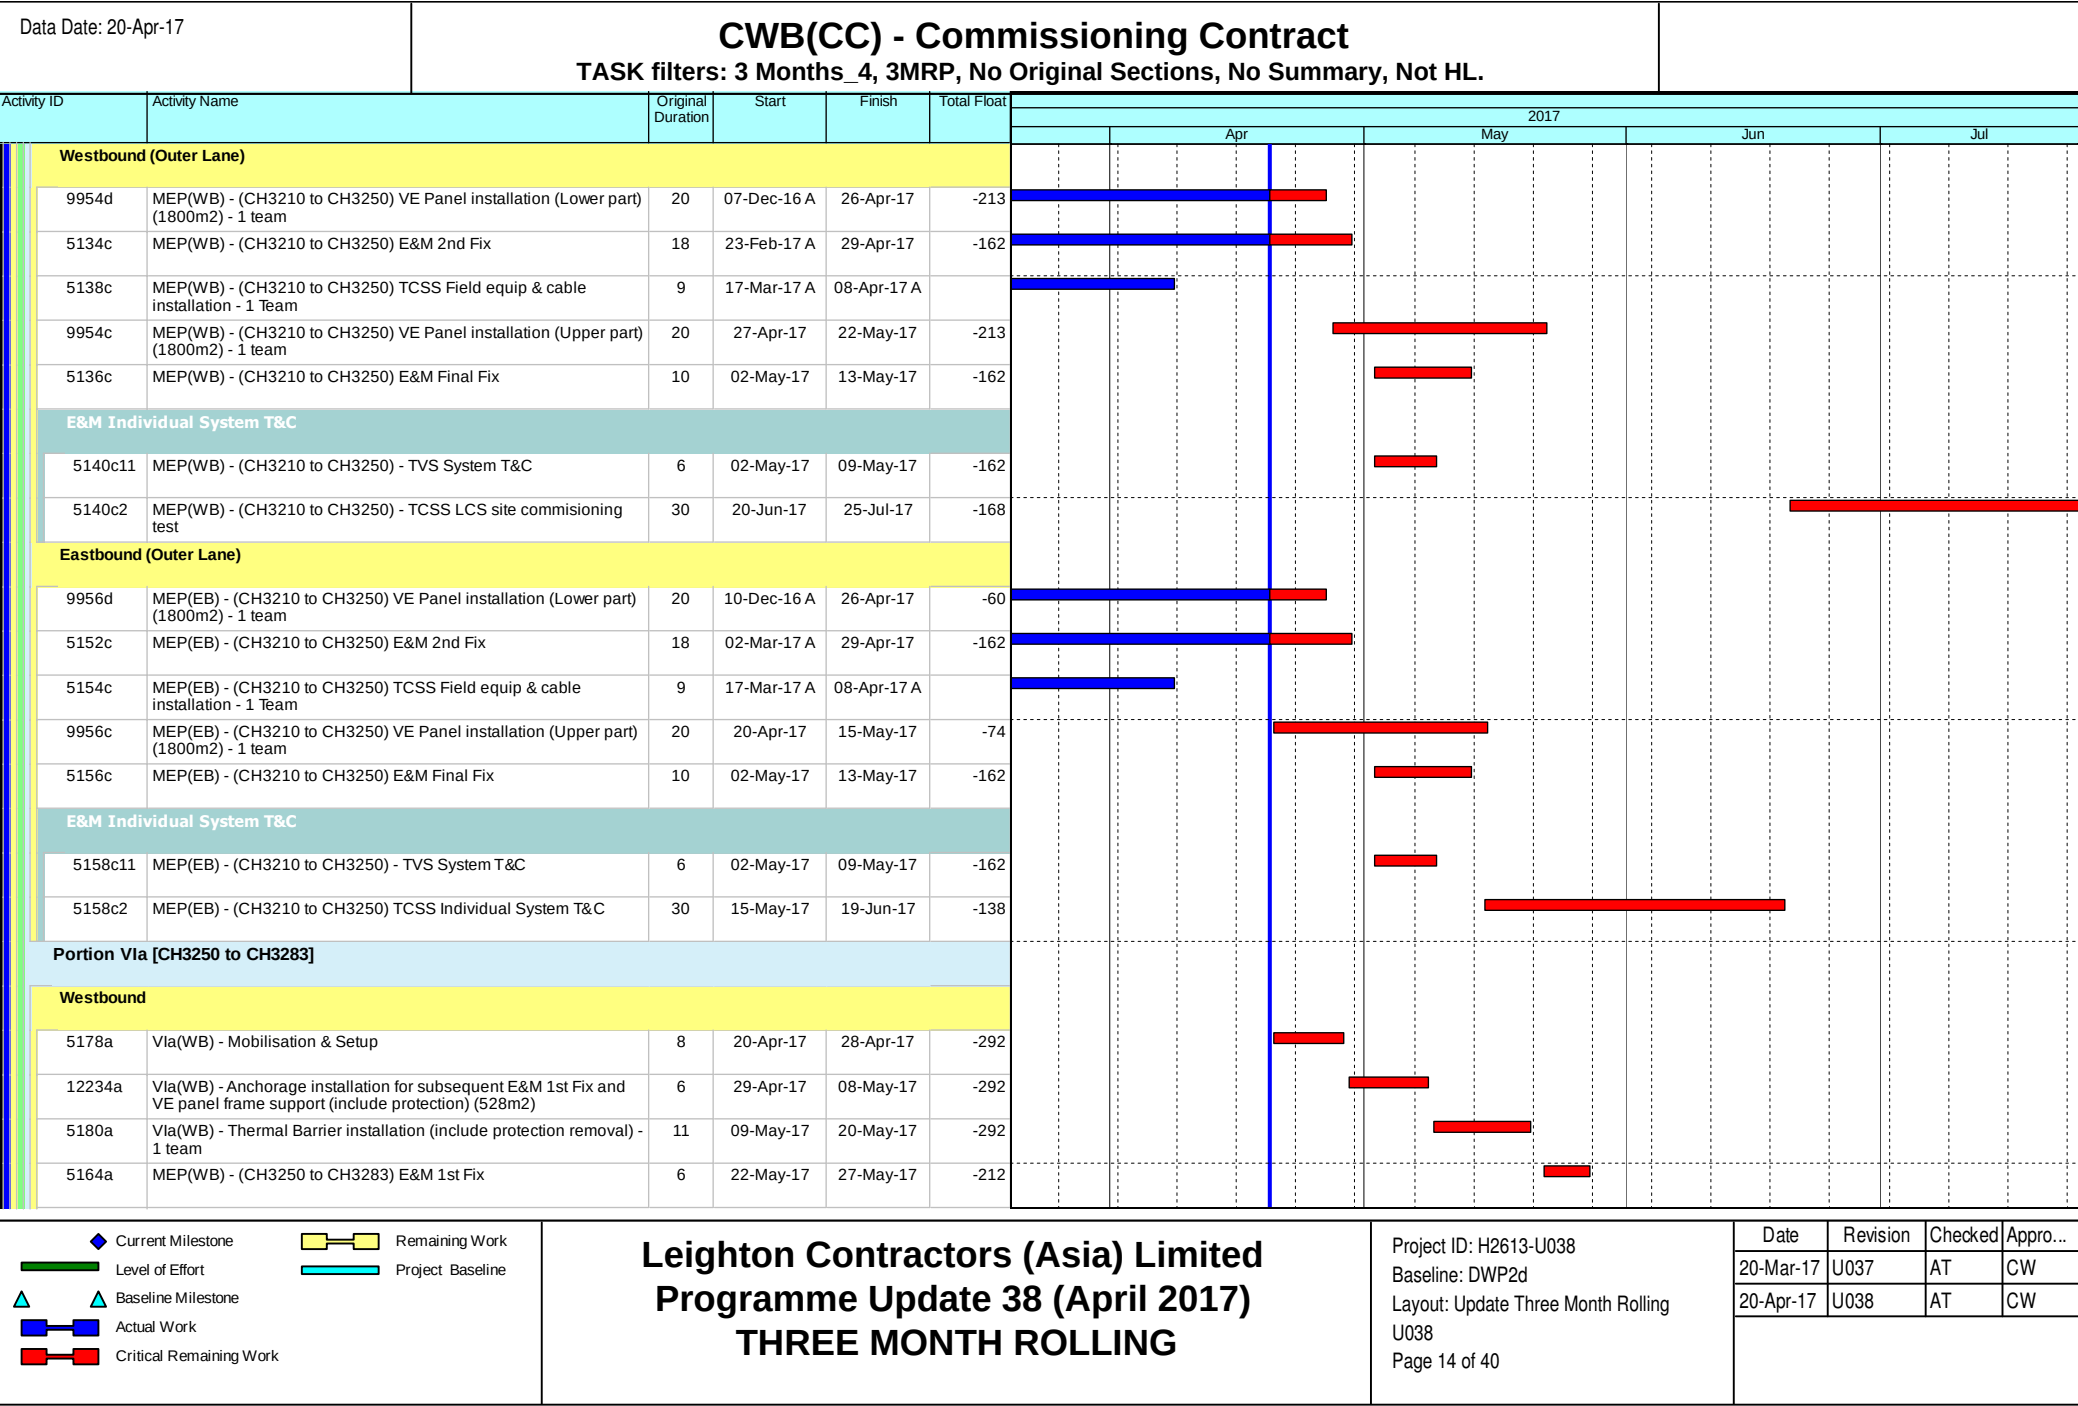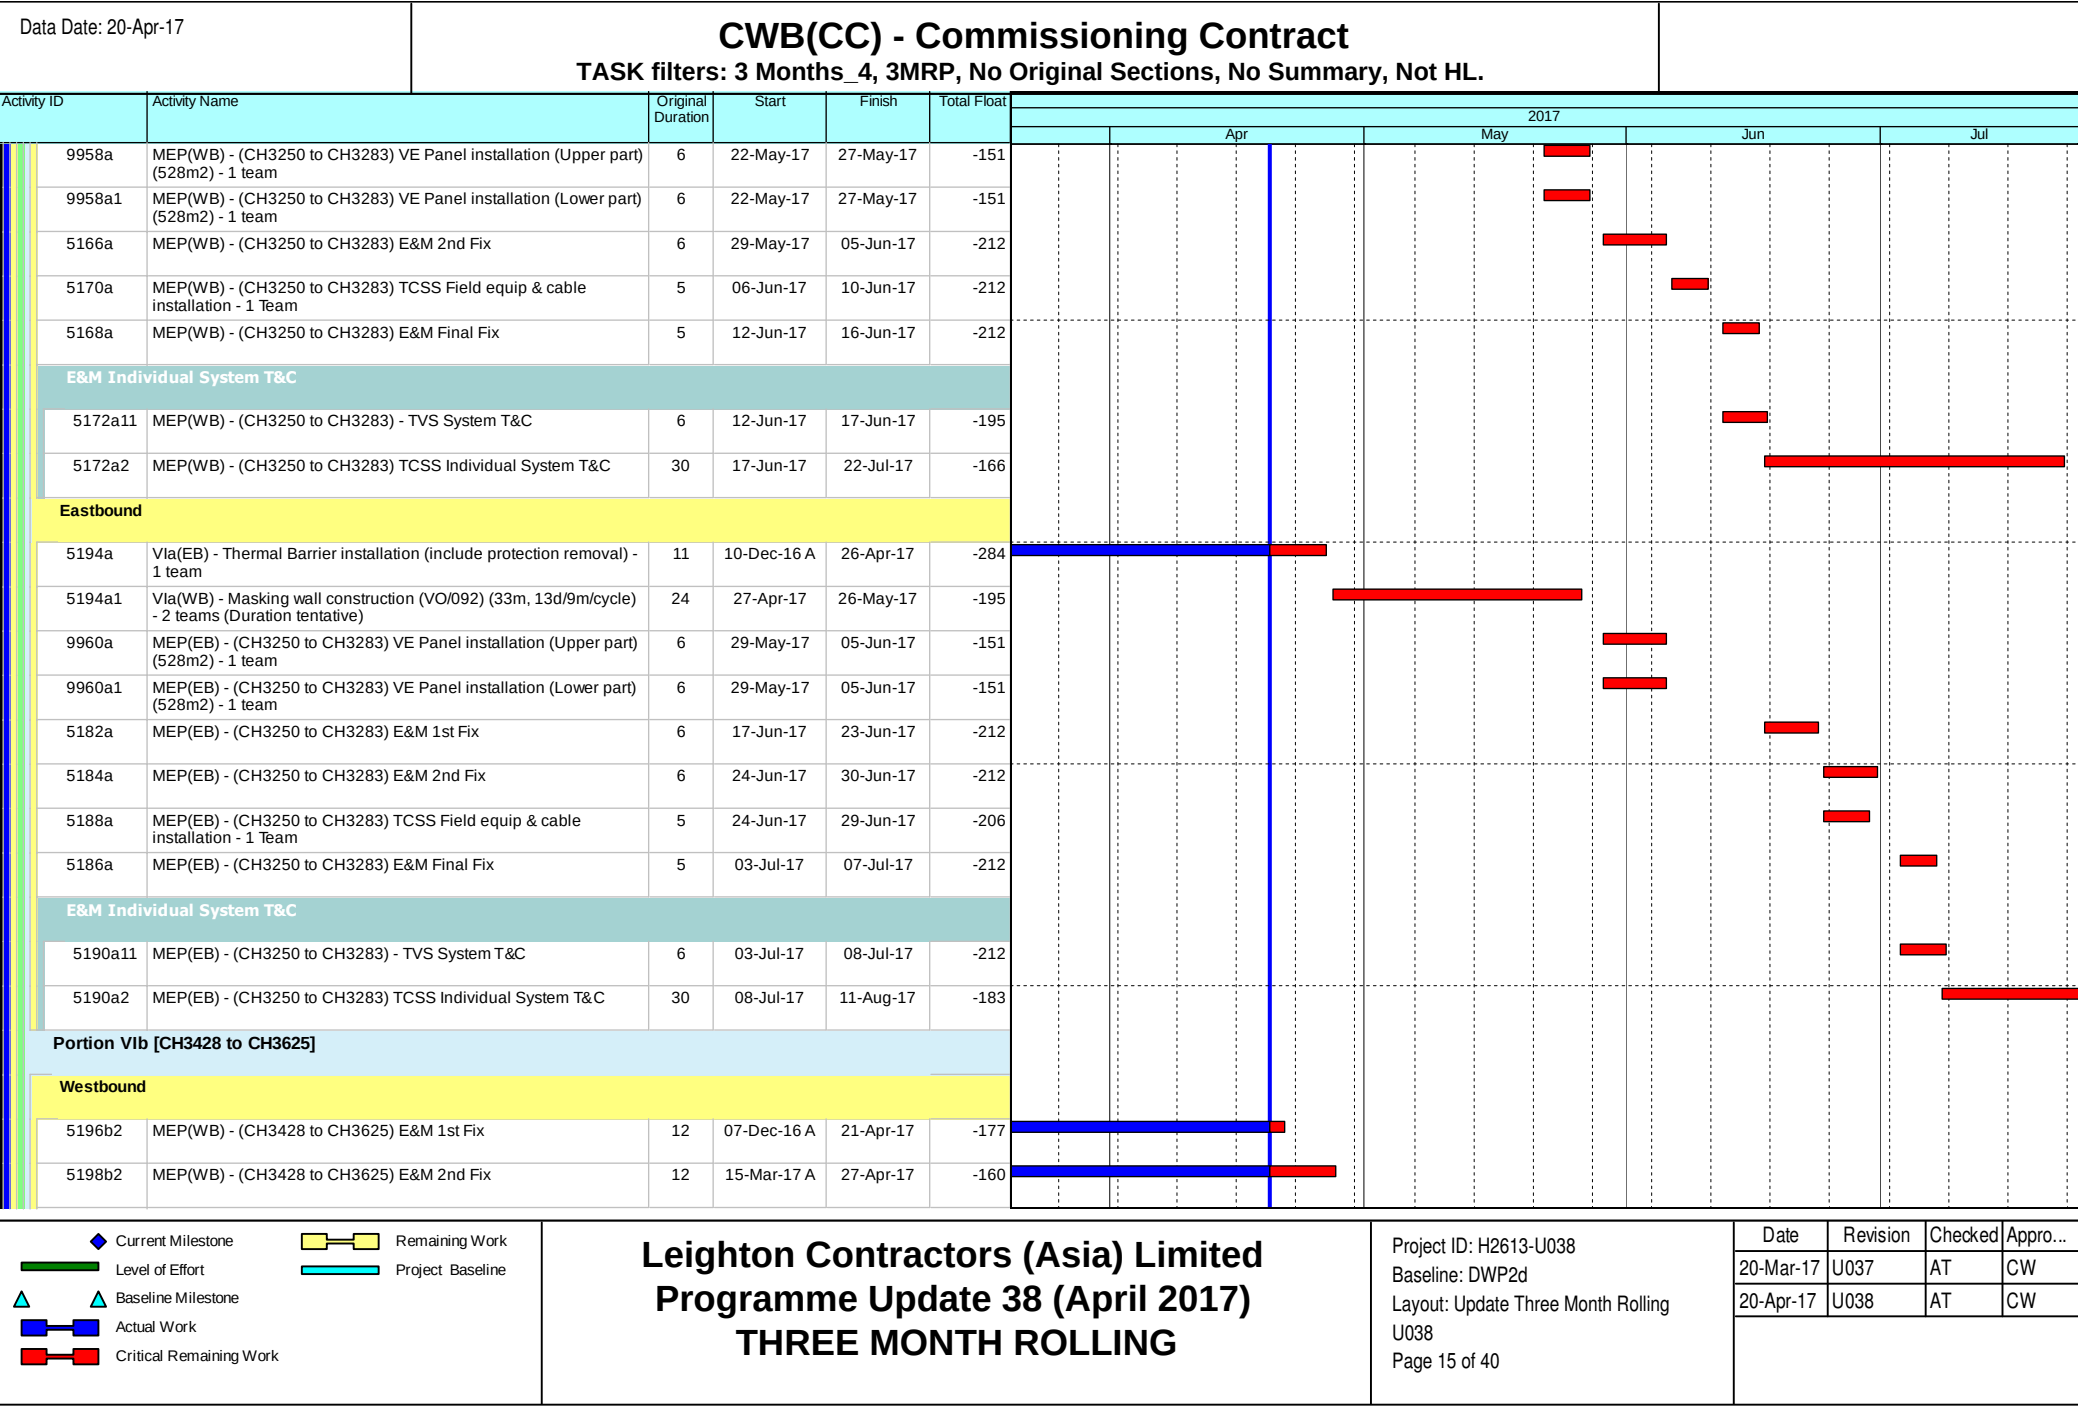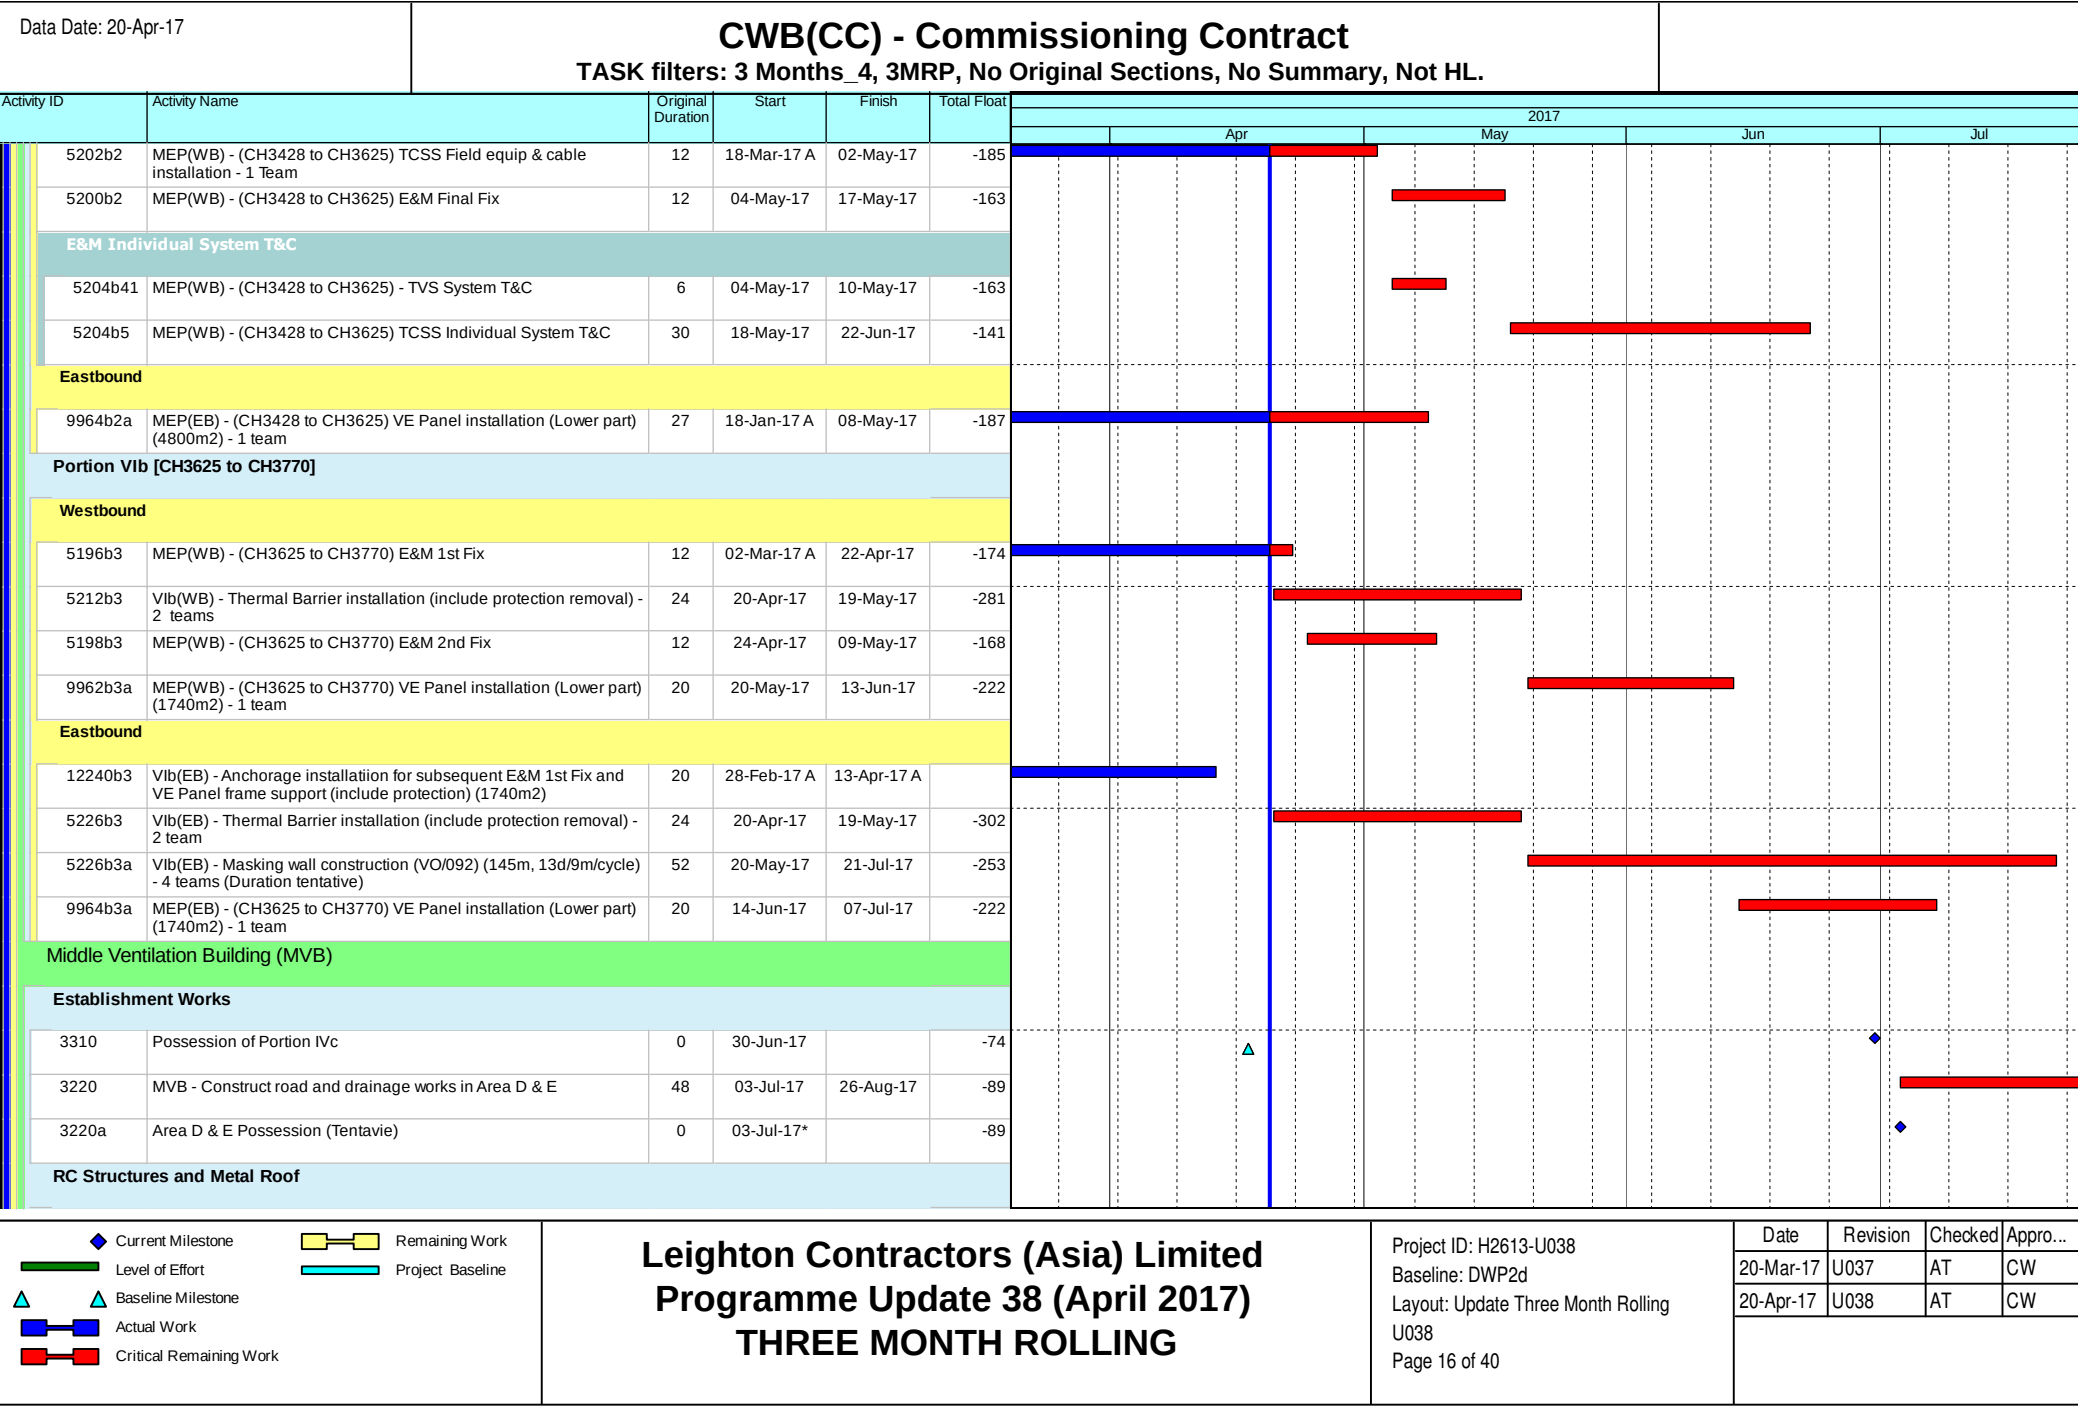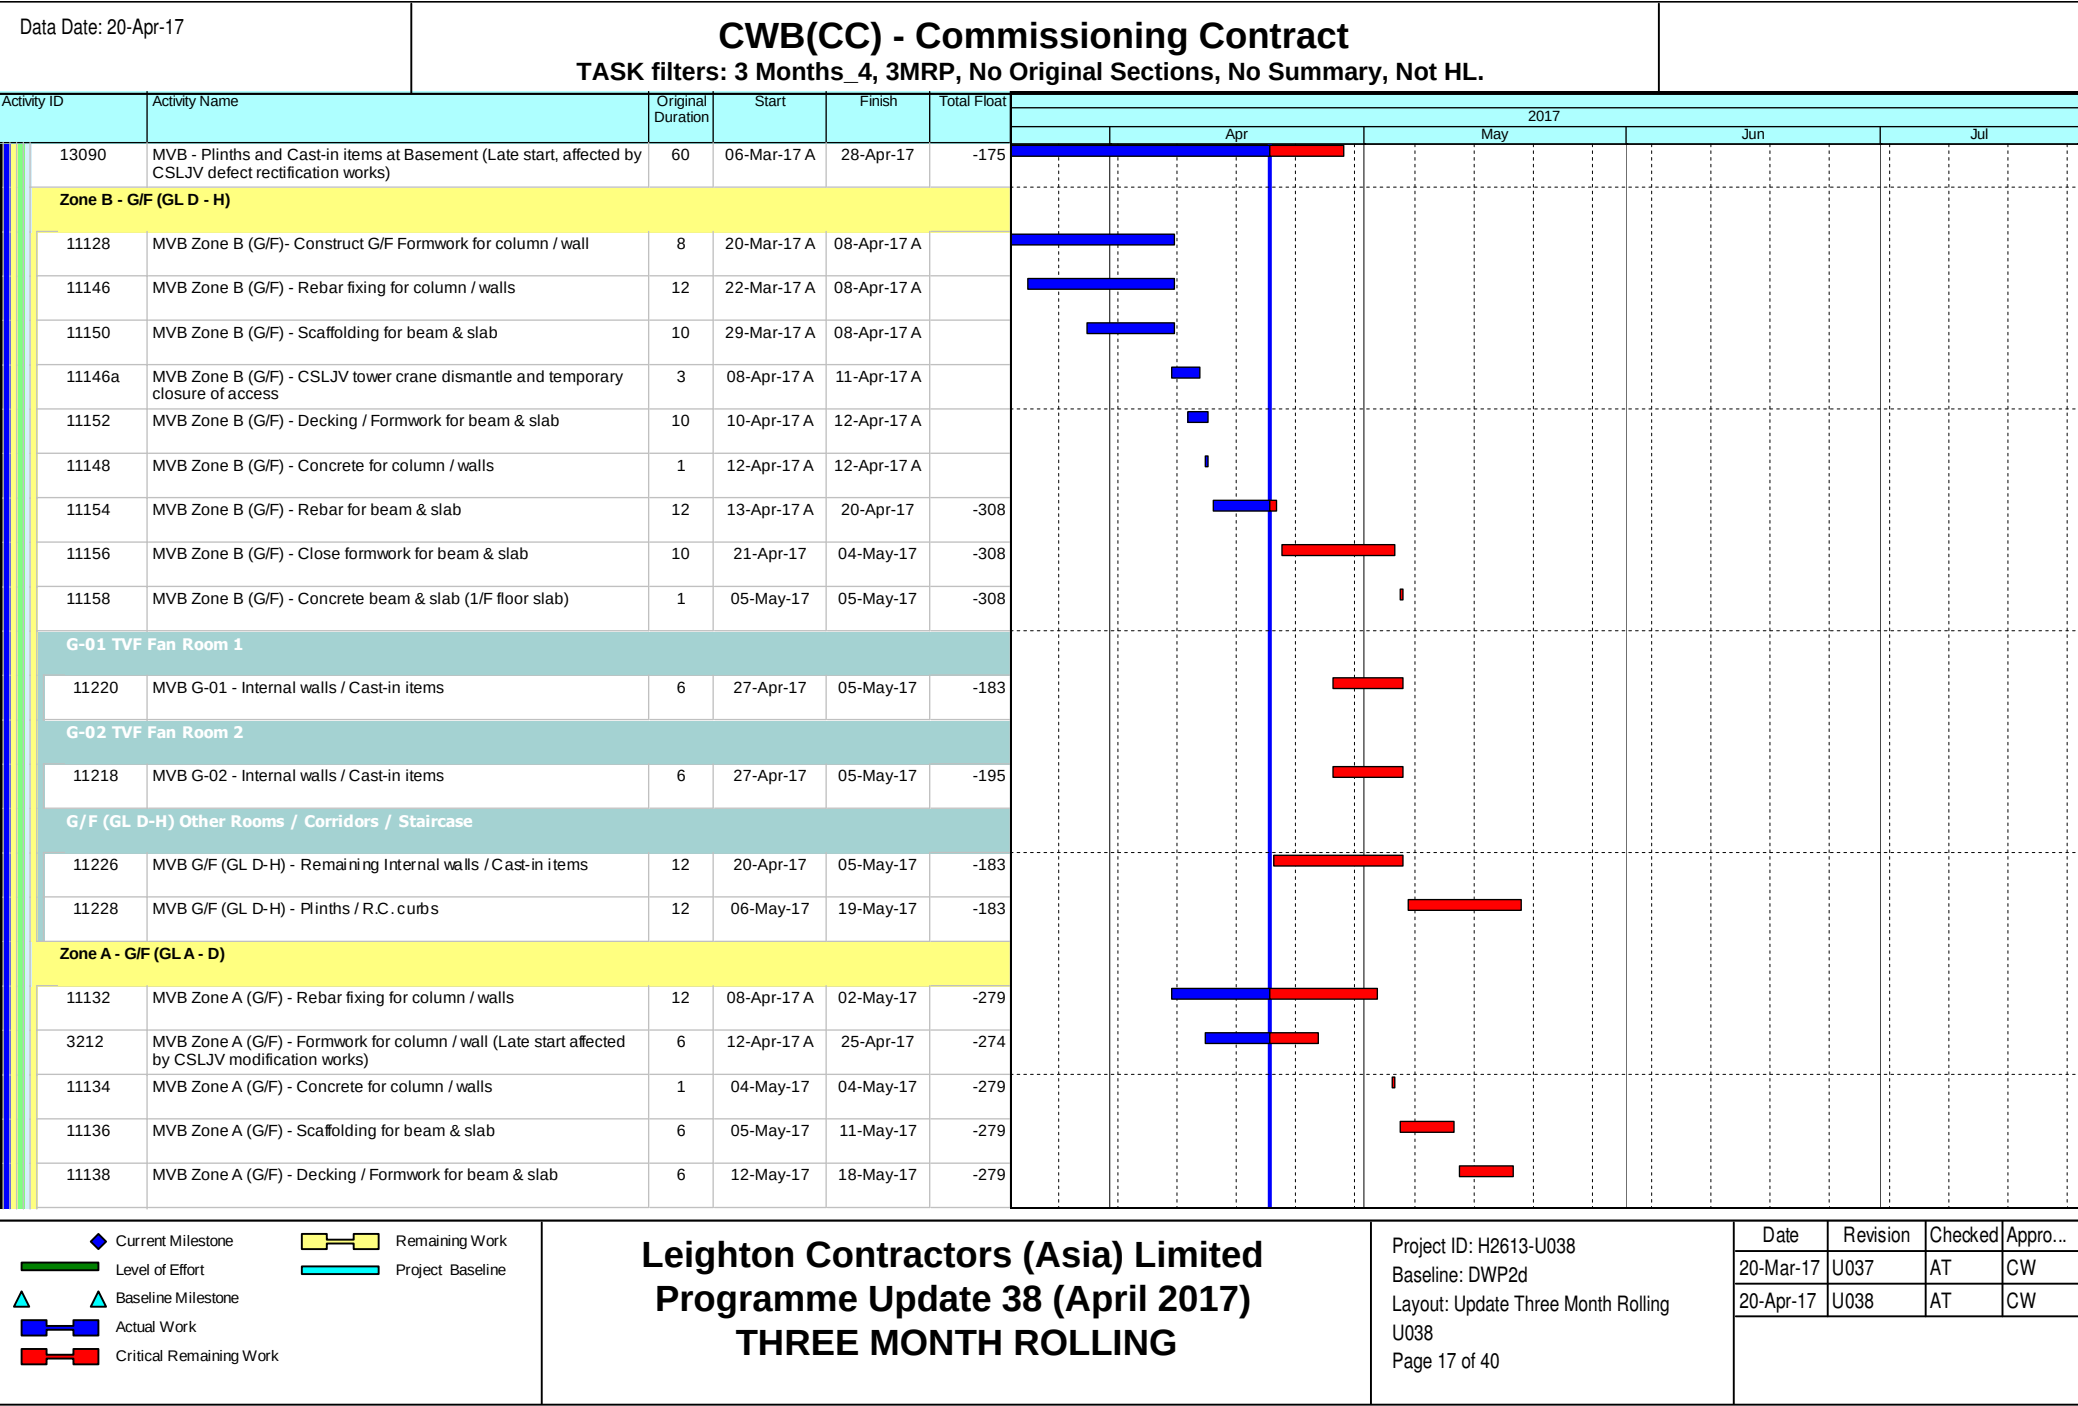







Data Date: 20-Apr-17		CWB(CC) - Commissioning Contract																
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																		
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017												
						Apr			May			Jun			Jul			
11140	MVB Zone A (G/F) - Rebar for beam & slab	10	19-May-17	31-May-17	-279													
11142	MVB Zone A (G/F) - Close formwork for beam & slab	6	01-Jun-17	07-Jun-17	-279													
11144	MVB Zone A (G/F) - Concrete beam & slab (1/F floor slab)	1	08-Jun-17	08-Jun-17	-279													
G-07 HKE/HV Switch Room 1																		
11210	MVB G-07 - Internal walls / Cast-in items	6	02-Jun-17	08-Jun-17	-231													
G-10 HKE/HV Switch Room 2																		
11208	MVB G-10 - Internal walls / Cast-in items	6	02-Jun-17	08-Jun-17	-219													
G-05 Transformer Room 1																		
11212	MVB G-05 - Internal walls / Cast-in items	6	02-Jun-17	08-Jun-17	-231													
G-08 Transformer Room 2																		
11214	MVB G-08 - Internal walls / Cast-in items	12	25-May-17	08-Jun-17	-213													
G-11 Fire Control Centre																		
11216	MVB G-11 - Internal walls / Cast-in items	12	25-May-17	08-Jun-17	-165													
G/F Other Rooms / Corridors / Staircase																		
11222	MVB G/F (GL A-D) - Remaining Internal walls / Cast-in items	24	11-May-17	08-Jun-17	-165													
11224	MVB G/F (GL A-D) - Plinths / R.C. curbs	12	09-Jun-17	22-Jun-17	-165													
Zone B - 1/F (GL D - H)																		
11176	MVB Zone B (1/F) - Formwork for column / wall	8	06-May-17	15-May-17	-308													
11178	MVB Zone B (1/F) - Rebar fixing for column / walls	12	16-May-17	29-May-17	-308													
11180	MVB Zone B (1/F) - Concrete for column / walls	1	31-May-17	31-May-17	-308													
11182	MVB Zone B (1/F) - Scaffolding for beam & slab	10	01-Jun-17	12-Jun-17	-308													
11184	MVB Zone B (1/F) - Decking / Formwork for beam & slab	10	13-Jun-17	23-Jun-17	-308													
11186	MVB Zone B (1/F) - Rebar for beam & slab	12	24-Jun-17	08-Jul-17	-308													
11188	MVB Zone B (1/F) - Close formwork for beam & slab	10	10-Jul-17	20-Jul-17	-308													

Current Milestone

Level of Effort

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING

Project ID: H2613-U038

Baseline: DWP2d

Layout: Update Three Month Rolling

U038

Page 18 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

◆ Current Milestone

▬ Level of Effort

▲ Baseline Milestone

▬ Actual Work

▬ Critical Remaining Work

▬ Remaining Work

▬ Project Baseline

Leighton Contractors (Asia) Limited
Programme Update 38 (April 2017)
THREE MONTH ROLLING

Project ID: H2613-U038

Baseline: DWP2d

Layout: Update Three Month Rolling

U038

Page 18 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

Data Date: 20-Apr-17		CWB(CC) - Commissioning Contract																
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																		
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017												
						Apr			May			Jun			Jul			
19030	MEP(MVB) - E&M 1st fixing	30	31-May-17	05-Jul-17	-163													
19032	MEP(MVB) - E&M 2nd fixing	24	06-Jul-17	02-Aug-17	-163													
Basement 2M (GL D - H)																		
TV Plenum																		
19036	MEP(MVB) - ABWF Works	12	31-May-17	13-Jun-17	-175													
19038	MEP(MVB) - E&M 1st fixing	30	14-Jun-17	19-Jul-17	-175													
Basement 1 (GL D - H)																		
General Area & Corridor																		
11312	MEP(MVB) - ABWF Works	12	29-Apr-17	15-May-17	-151													
11314	MEP(MVB) - E&M 1st fixing	30	16-May-17	20-Jun-17	-151													
11316	MEP(MVB) - E&M 2nd fixing	24	21-Jun-17	19-Jul-17	-151													
Basement 1 (GLA - D)																		
MCC Room 1 (B1-04)																		
11280	MVB - ABWF works for MCC Room 1	12	01-Jun-17	14-Jun-17	-258													
11282	MEP(MVB) - E&M 1st fixing	12	15-Jun-17	28-Jun-17	-204													
12346	APS(MVB) - E&M 2nd fixing	12	29-Jun-17	13-Jul-17	-204													
11284	MEP(MVB) - MCC installation	12	14-Jul-17	27-Jul-17	-158													
UPS Room 1 (B1-11)																		
11288	MVB - ABWF works for UPS Room	12	15-Jun-17	28-Jun-17	-258													
11290	MEP(MVB) - E&M 1st fixing	12	29-Jun-17	13-Jul-17	-212													
12348	APS(MVB) - E&M 2nd fixing	12	14-Jul-17	27-Jul-17	-212													
MCC Room 2 (B1-07)																		
11304	MVB - ABWF works for MCC Room 2	12	29-Jun-17	13-Jul-17	-258													
11306	MEP(MVB) - E&M 1st fixing	12	14-Jul-17	27-Jul-17	-212													

Current Milestone

Level of Effort

Baseline Milestone

Actual Work

Critical Remaining Work

Remaining Work

Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING

Project ID: H2613-U038

Baseline: DWP2d

Layout: Update Three Month Rolling

U038

Page 20 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

◆ Current Milestone

▬ Level of Effort

▲ Baseline Milestone

▬ Actual Work

▬ Critical Remaining Work

▬ Remaining Work

▬ Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING

Project ID: H2613-U038

Baseline: DWP2d


Layout: Update Three Month Rolling


U038


Page 20 of 40


Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

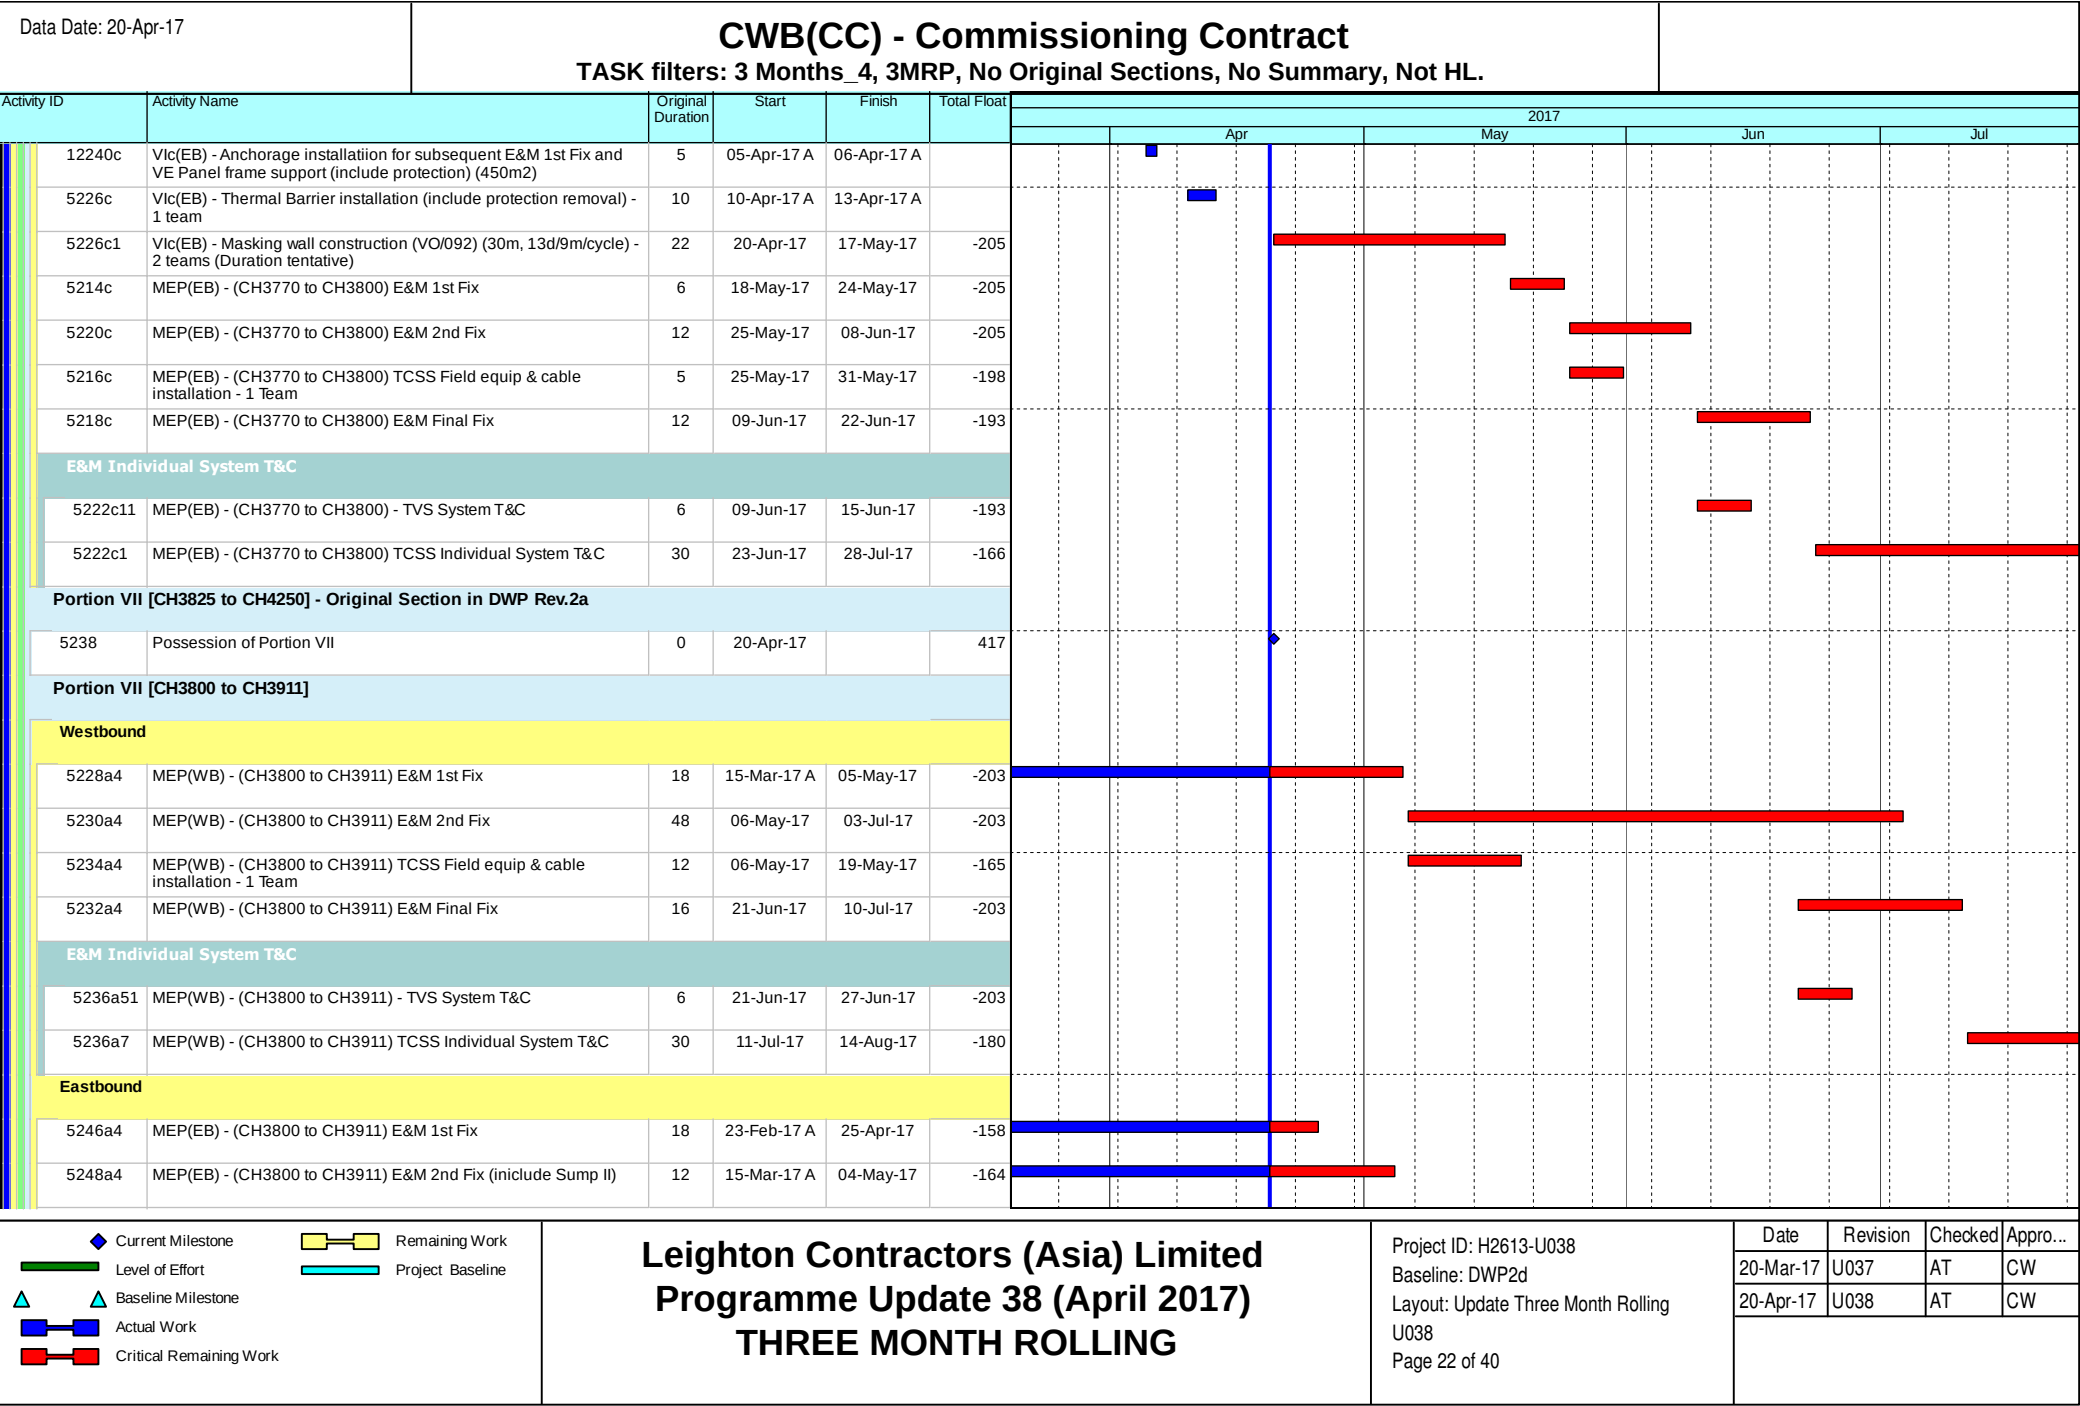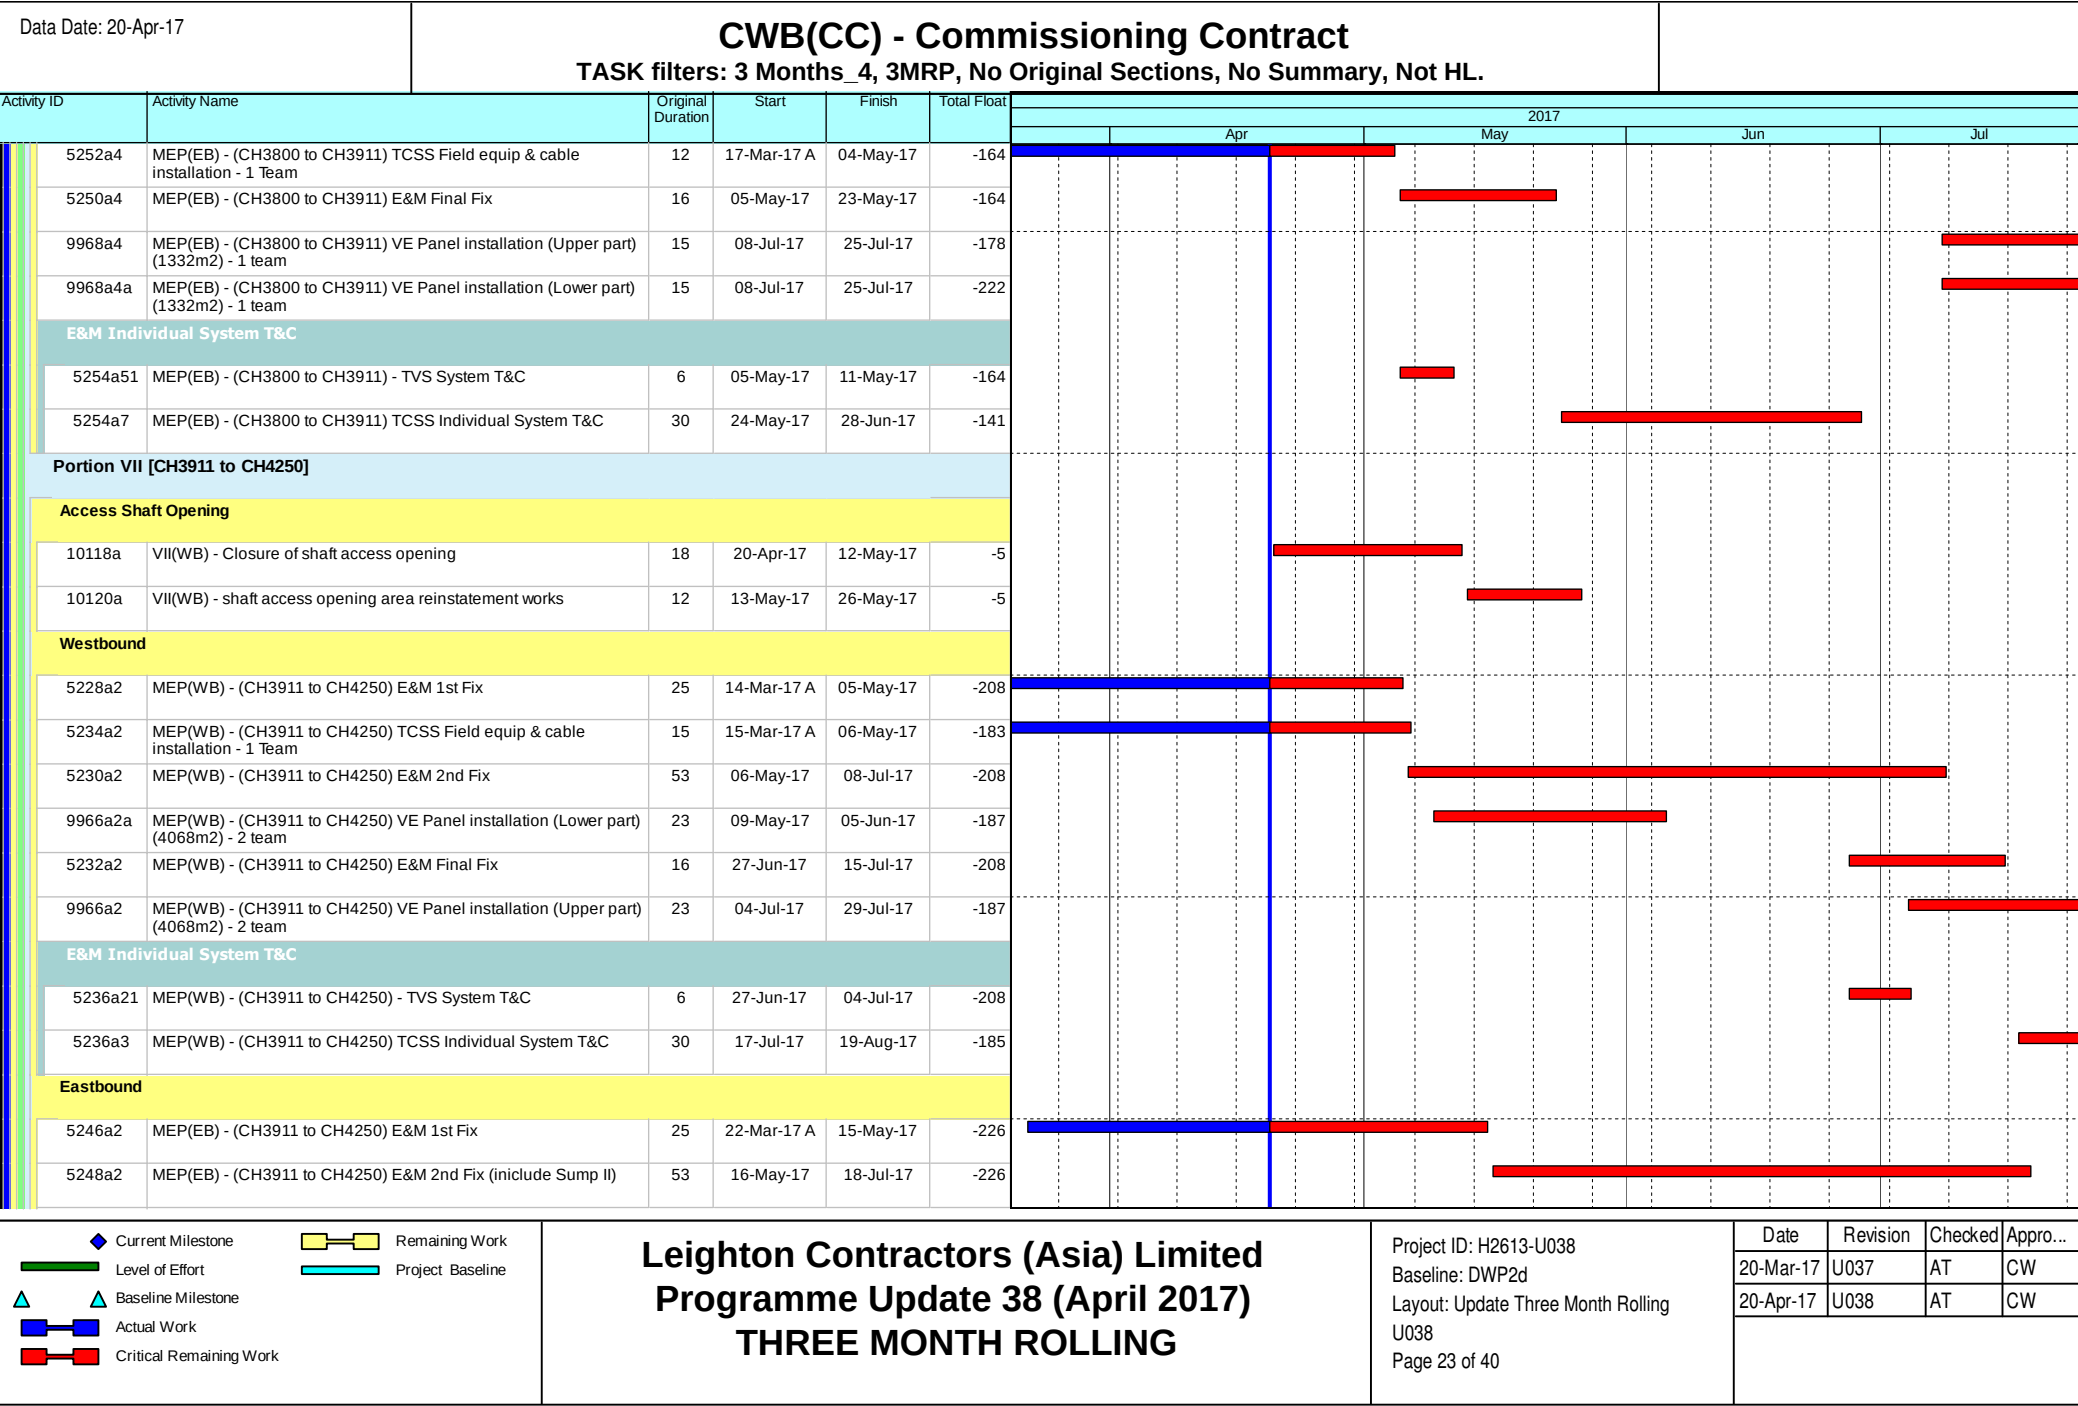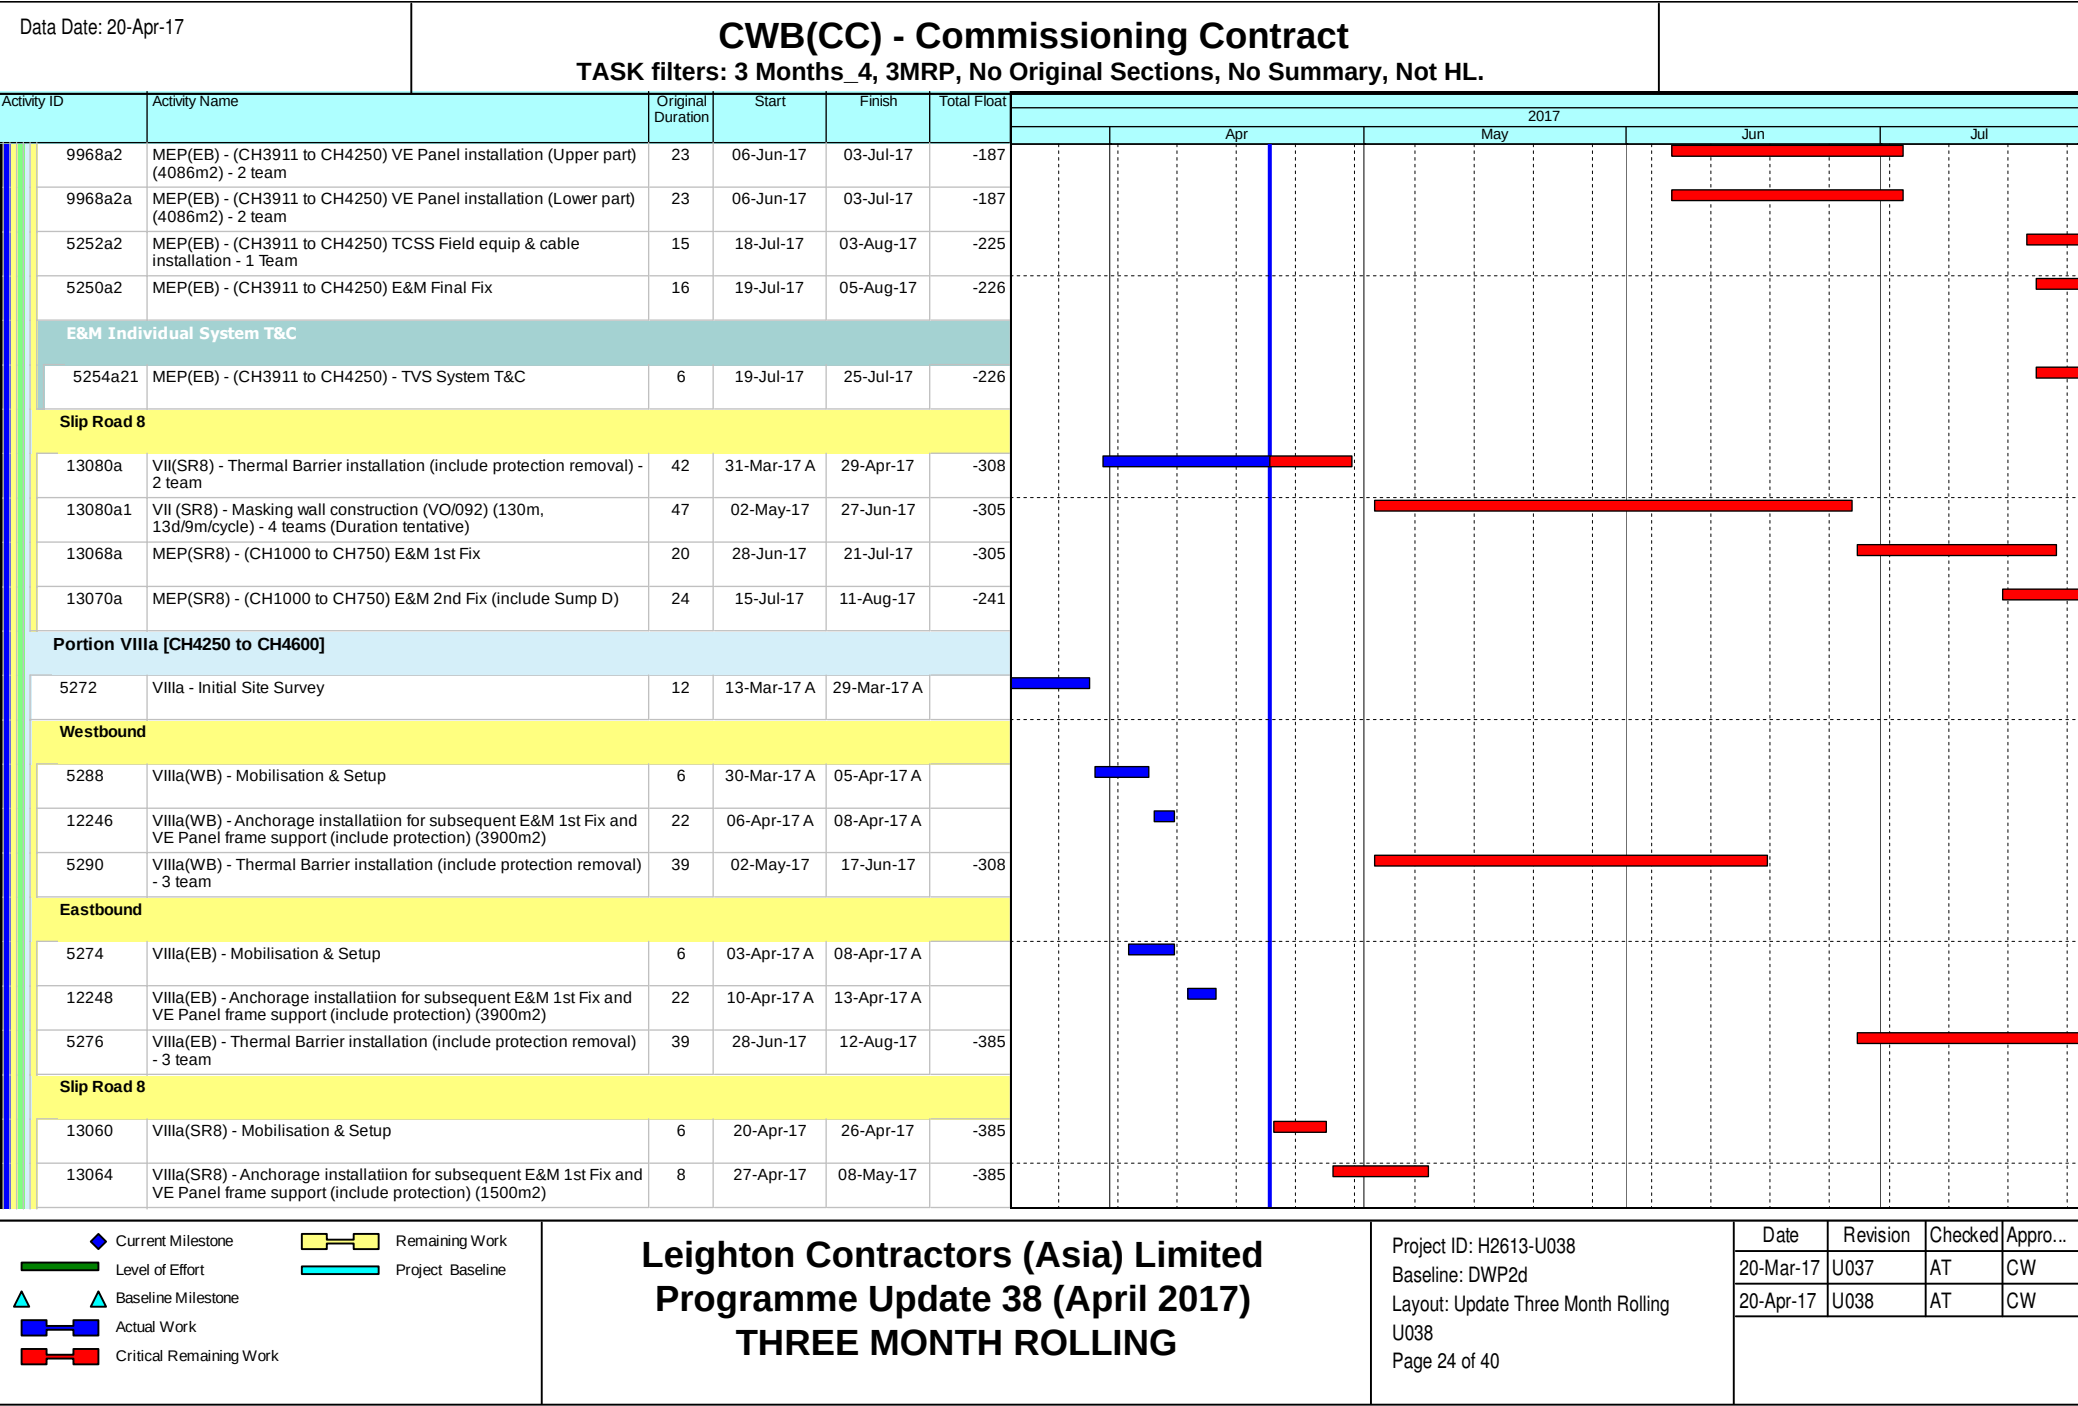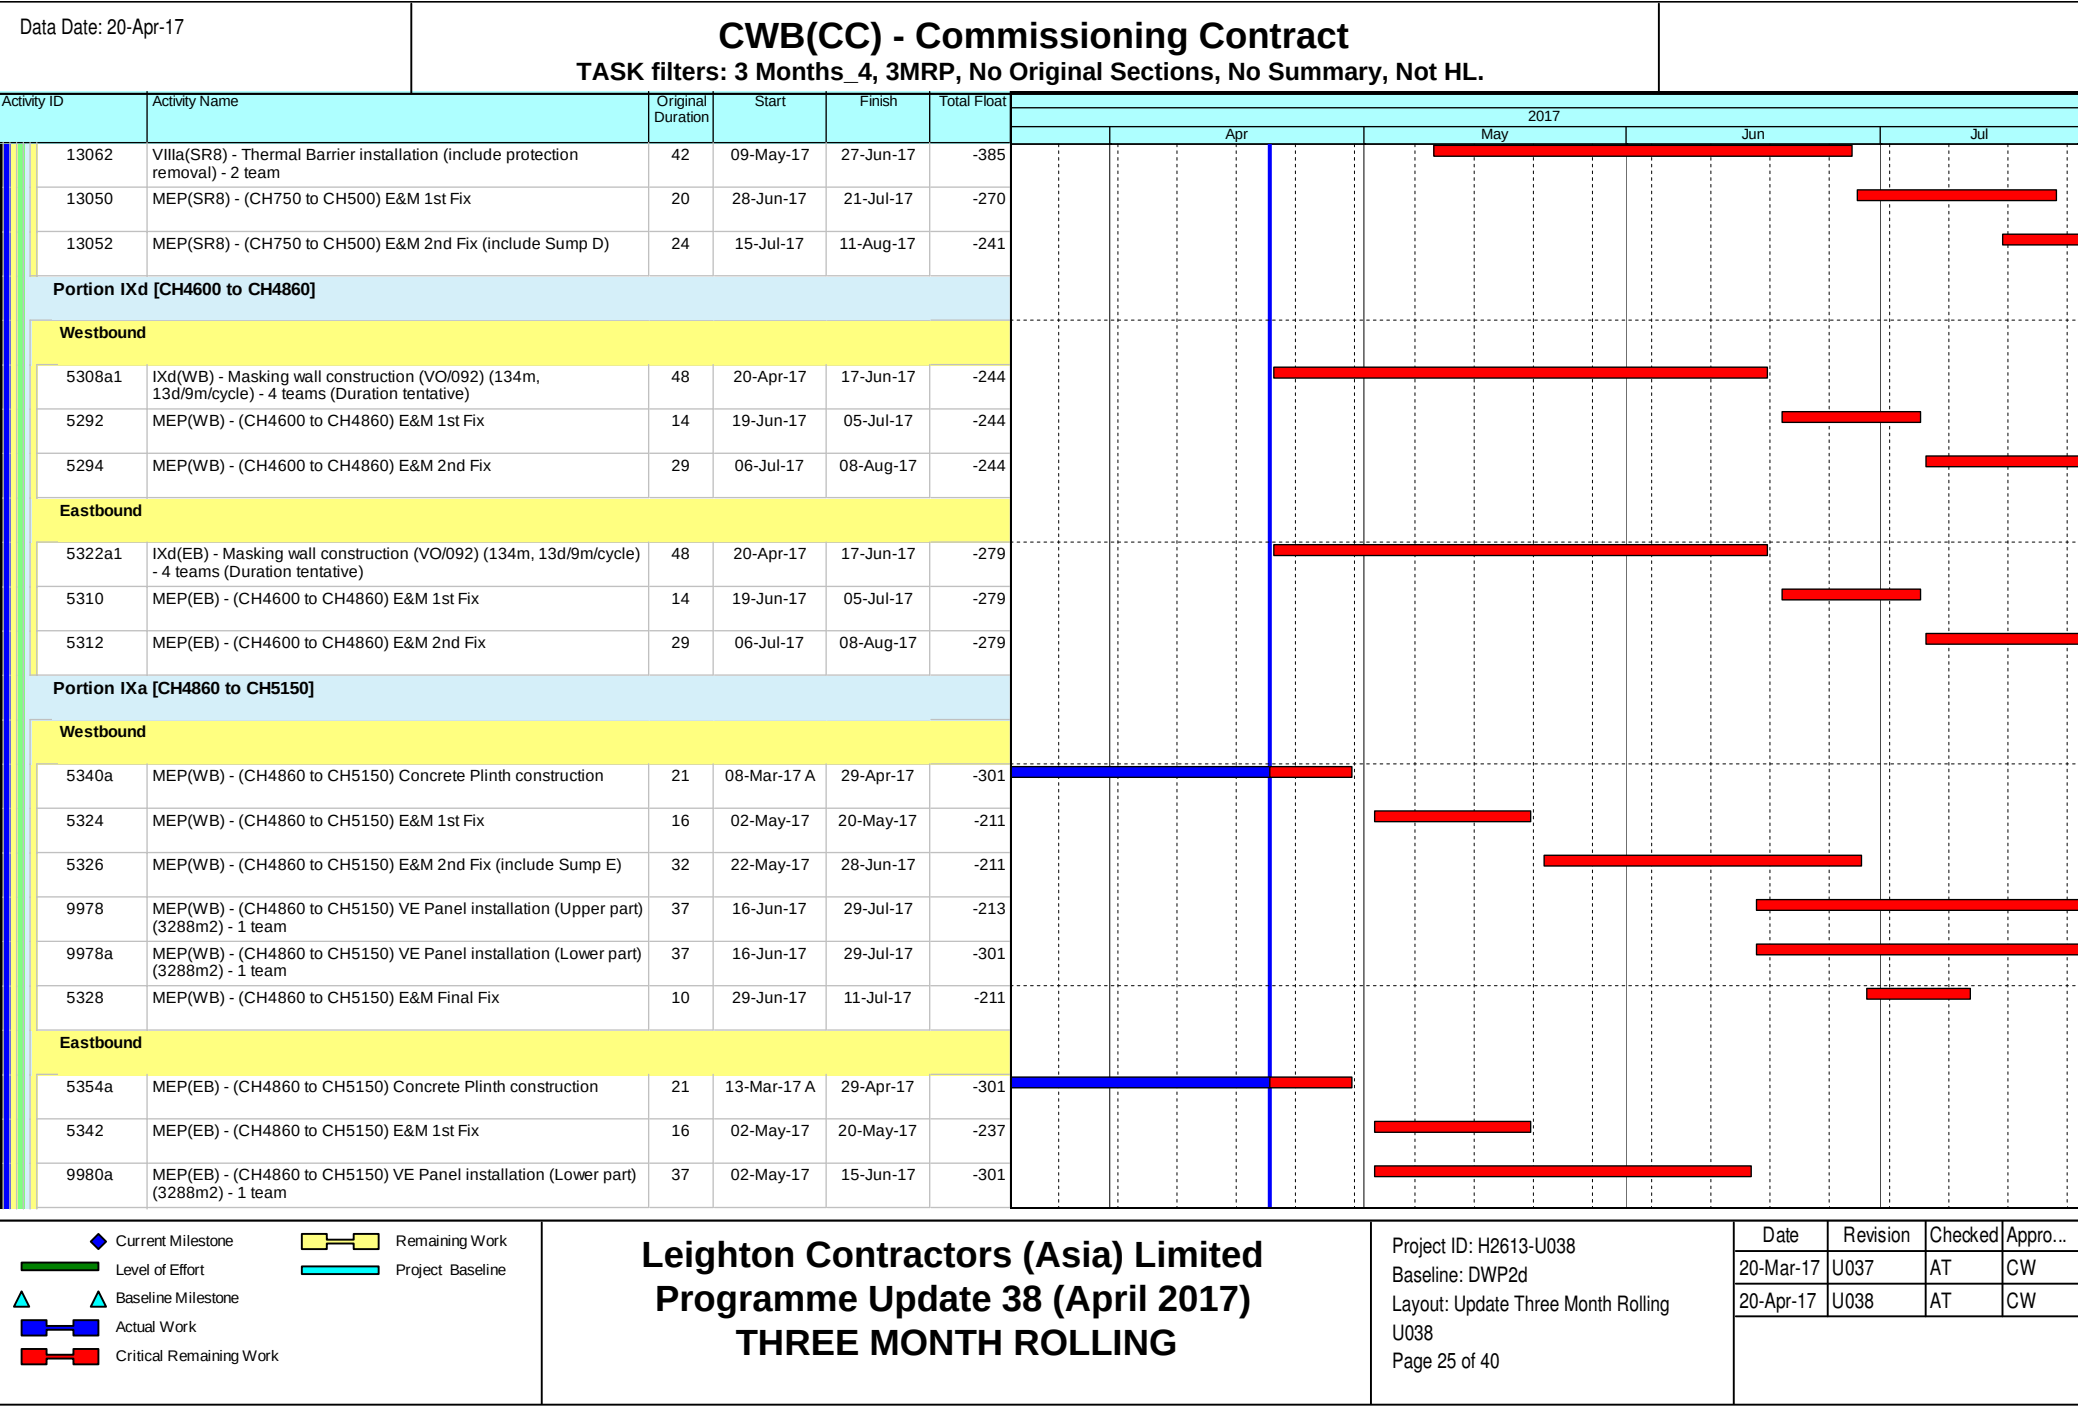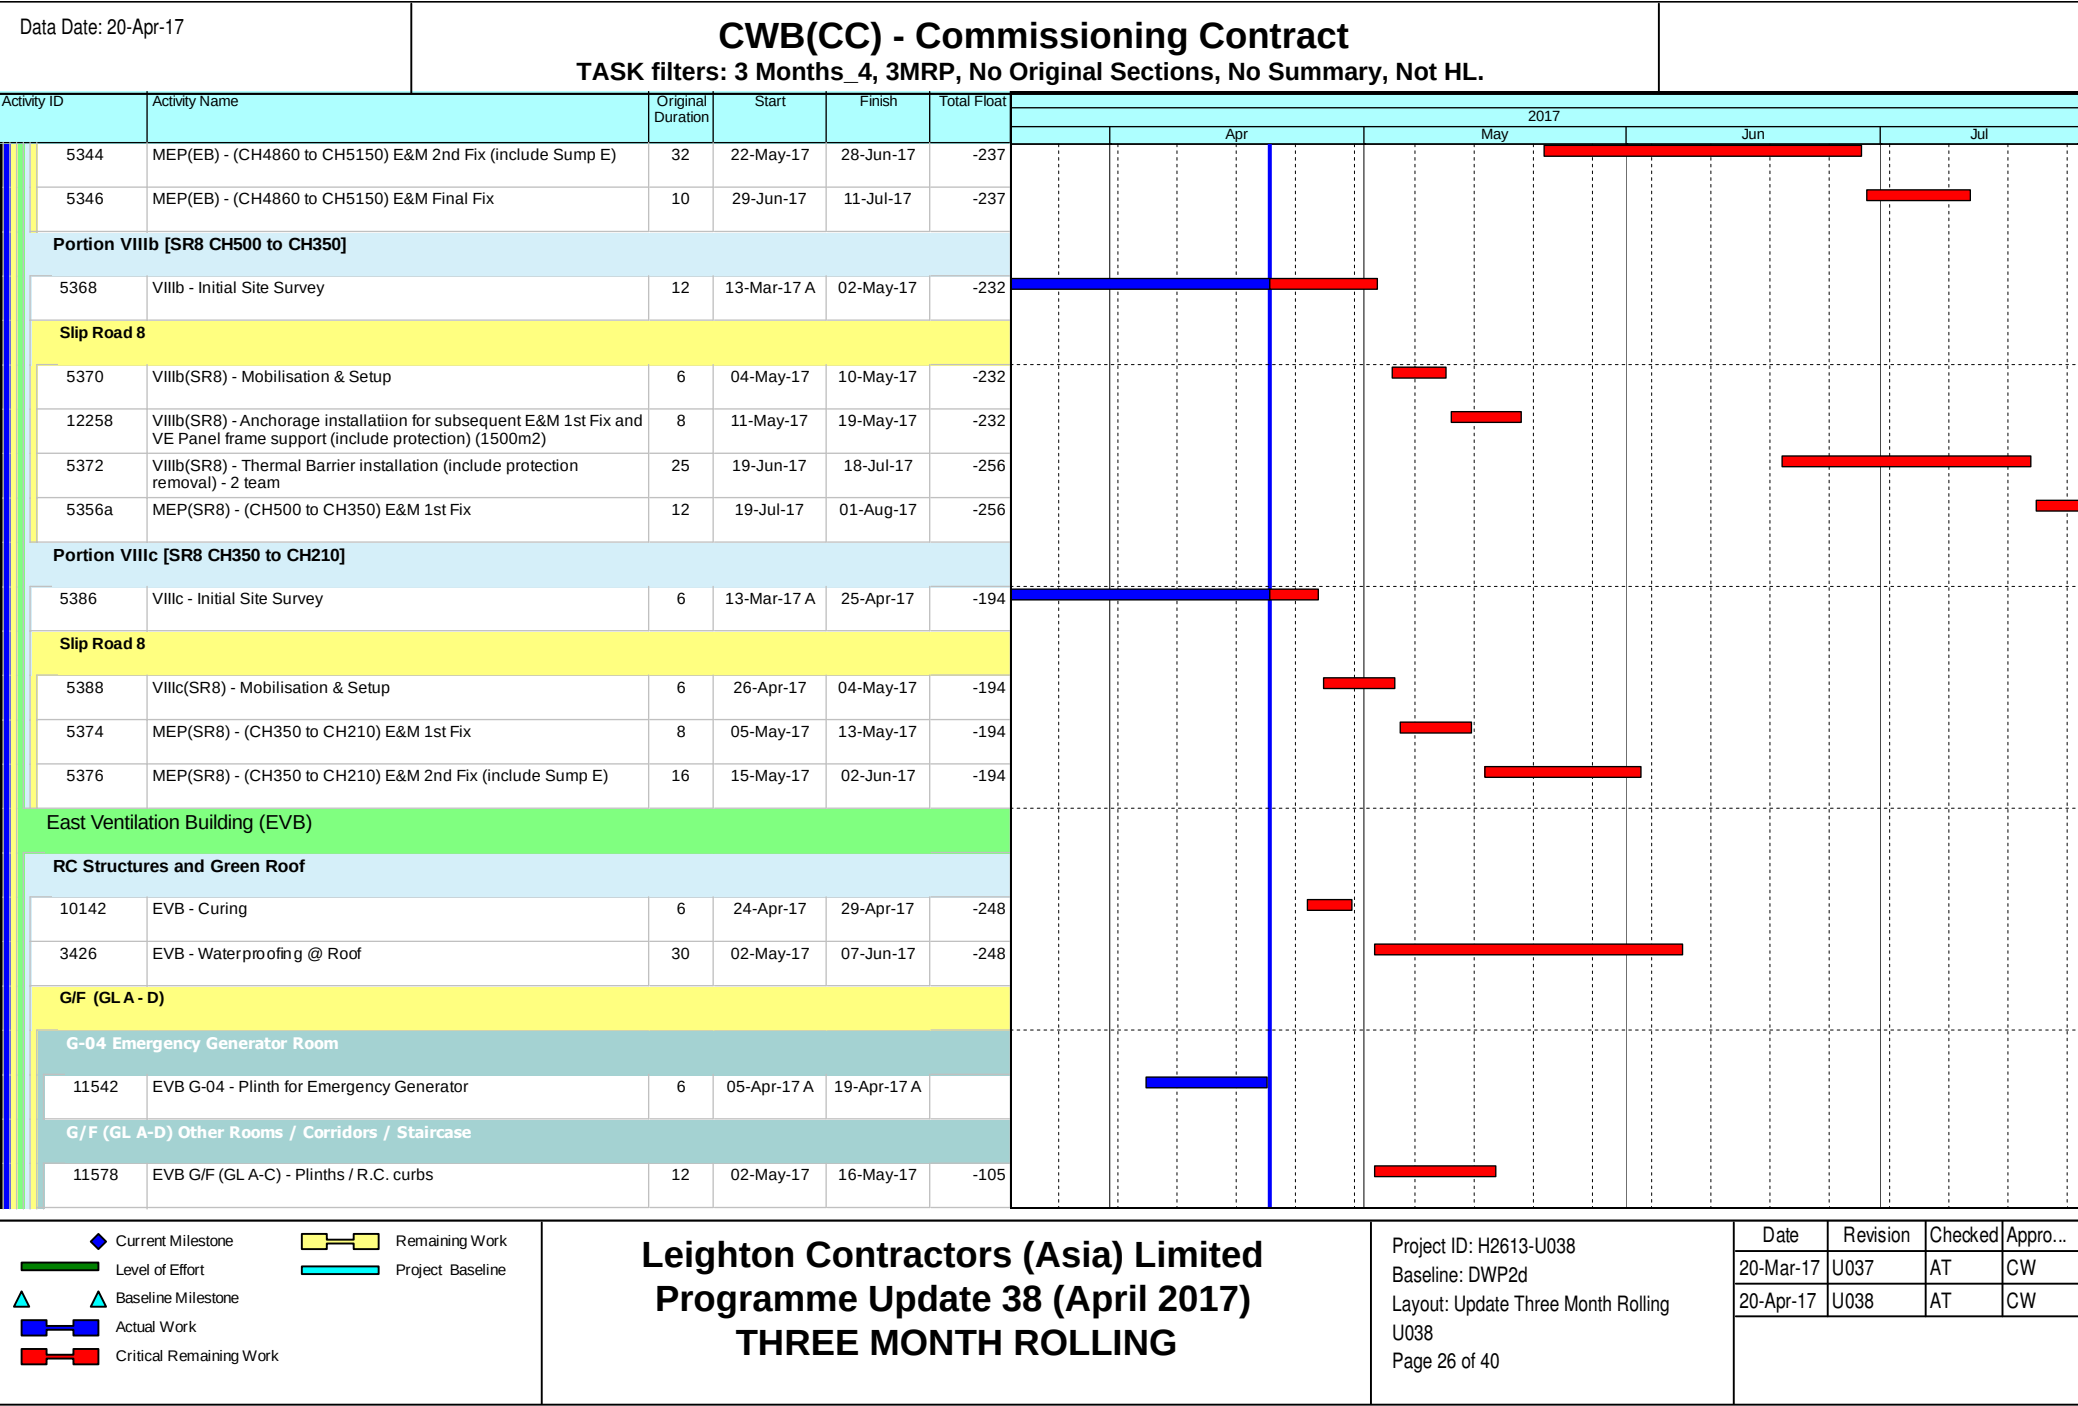
[illegible]

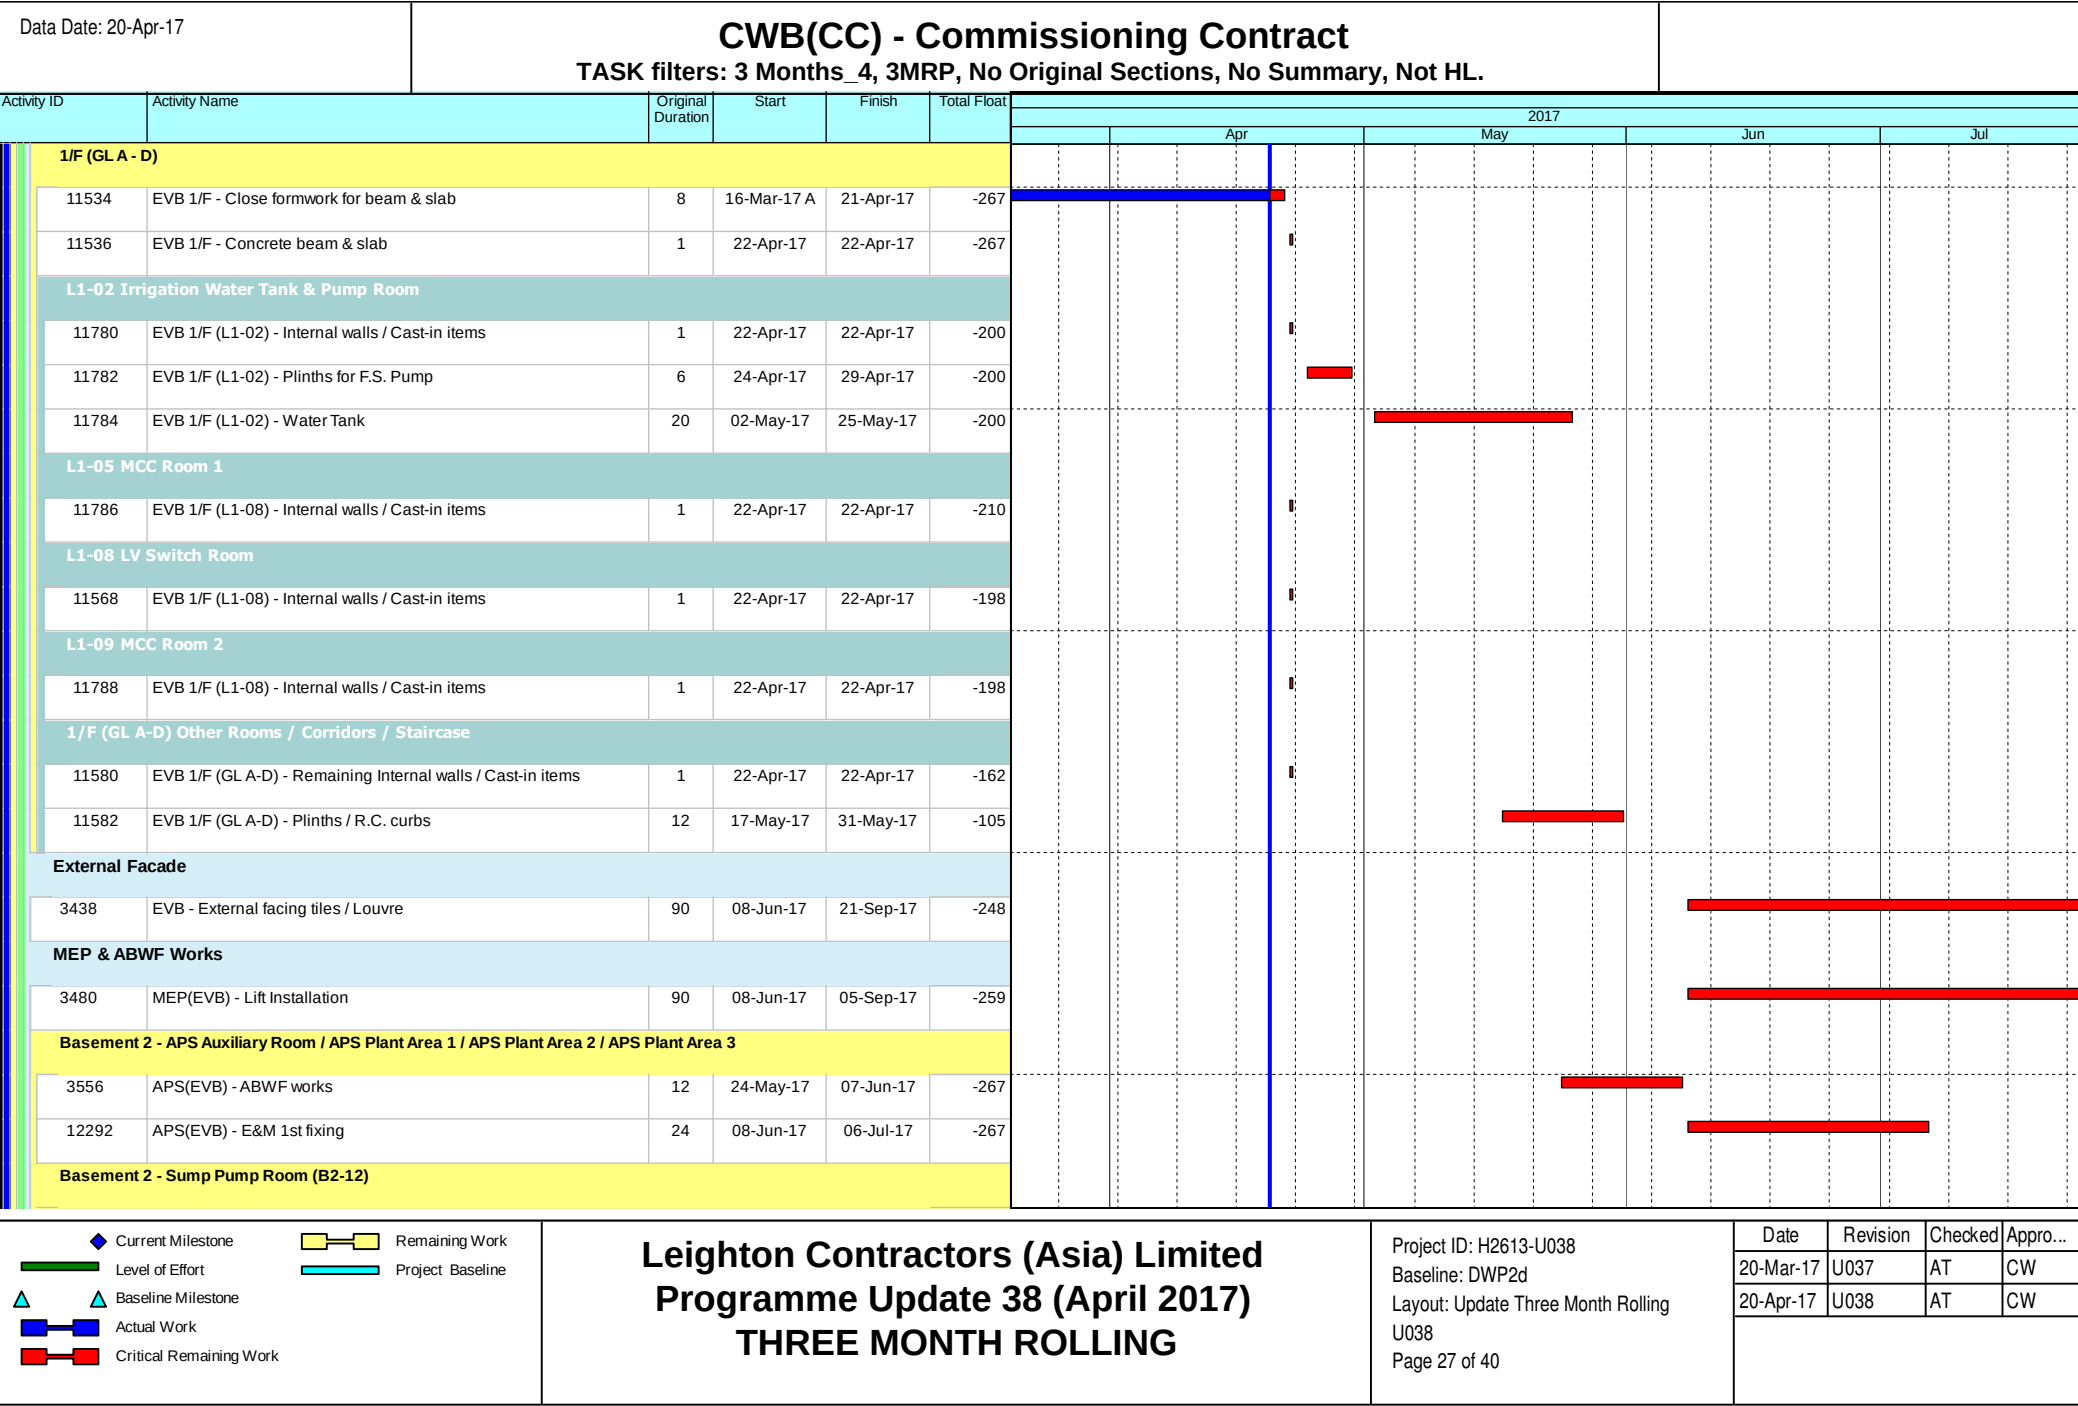


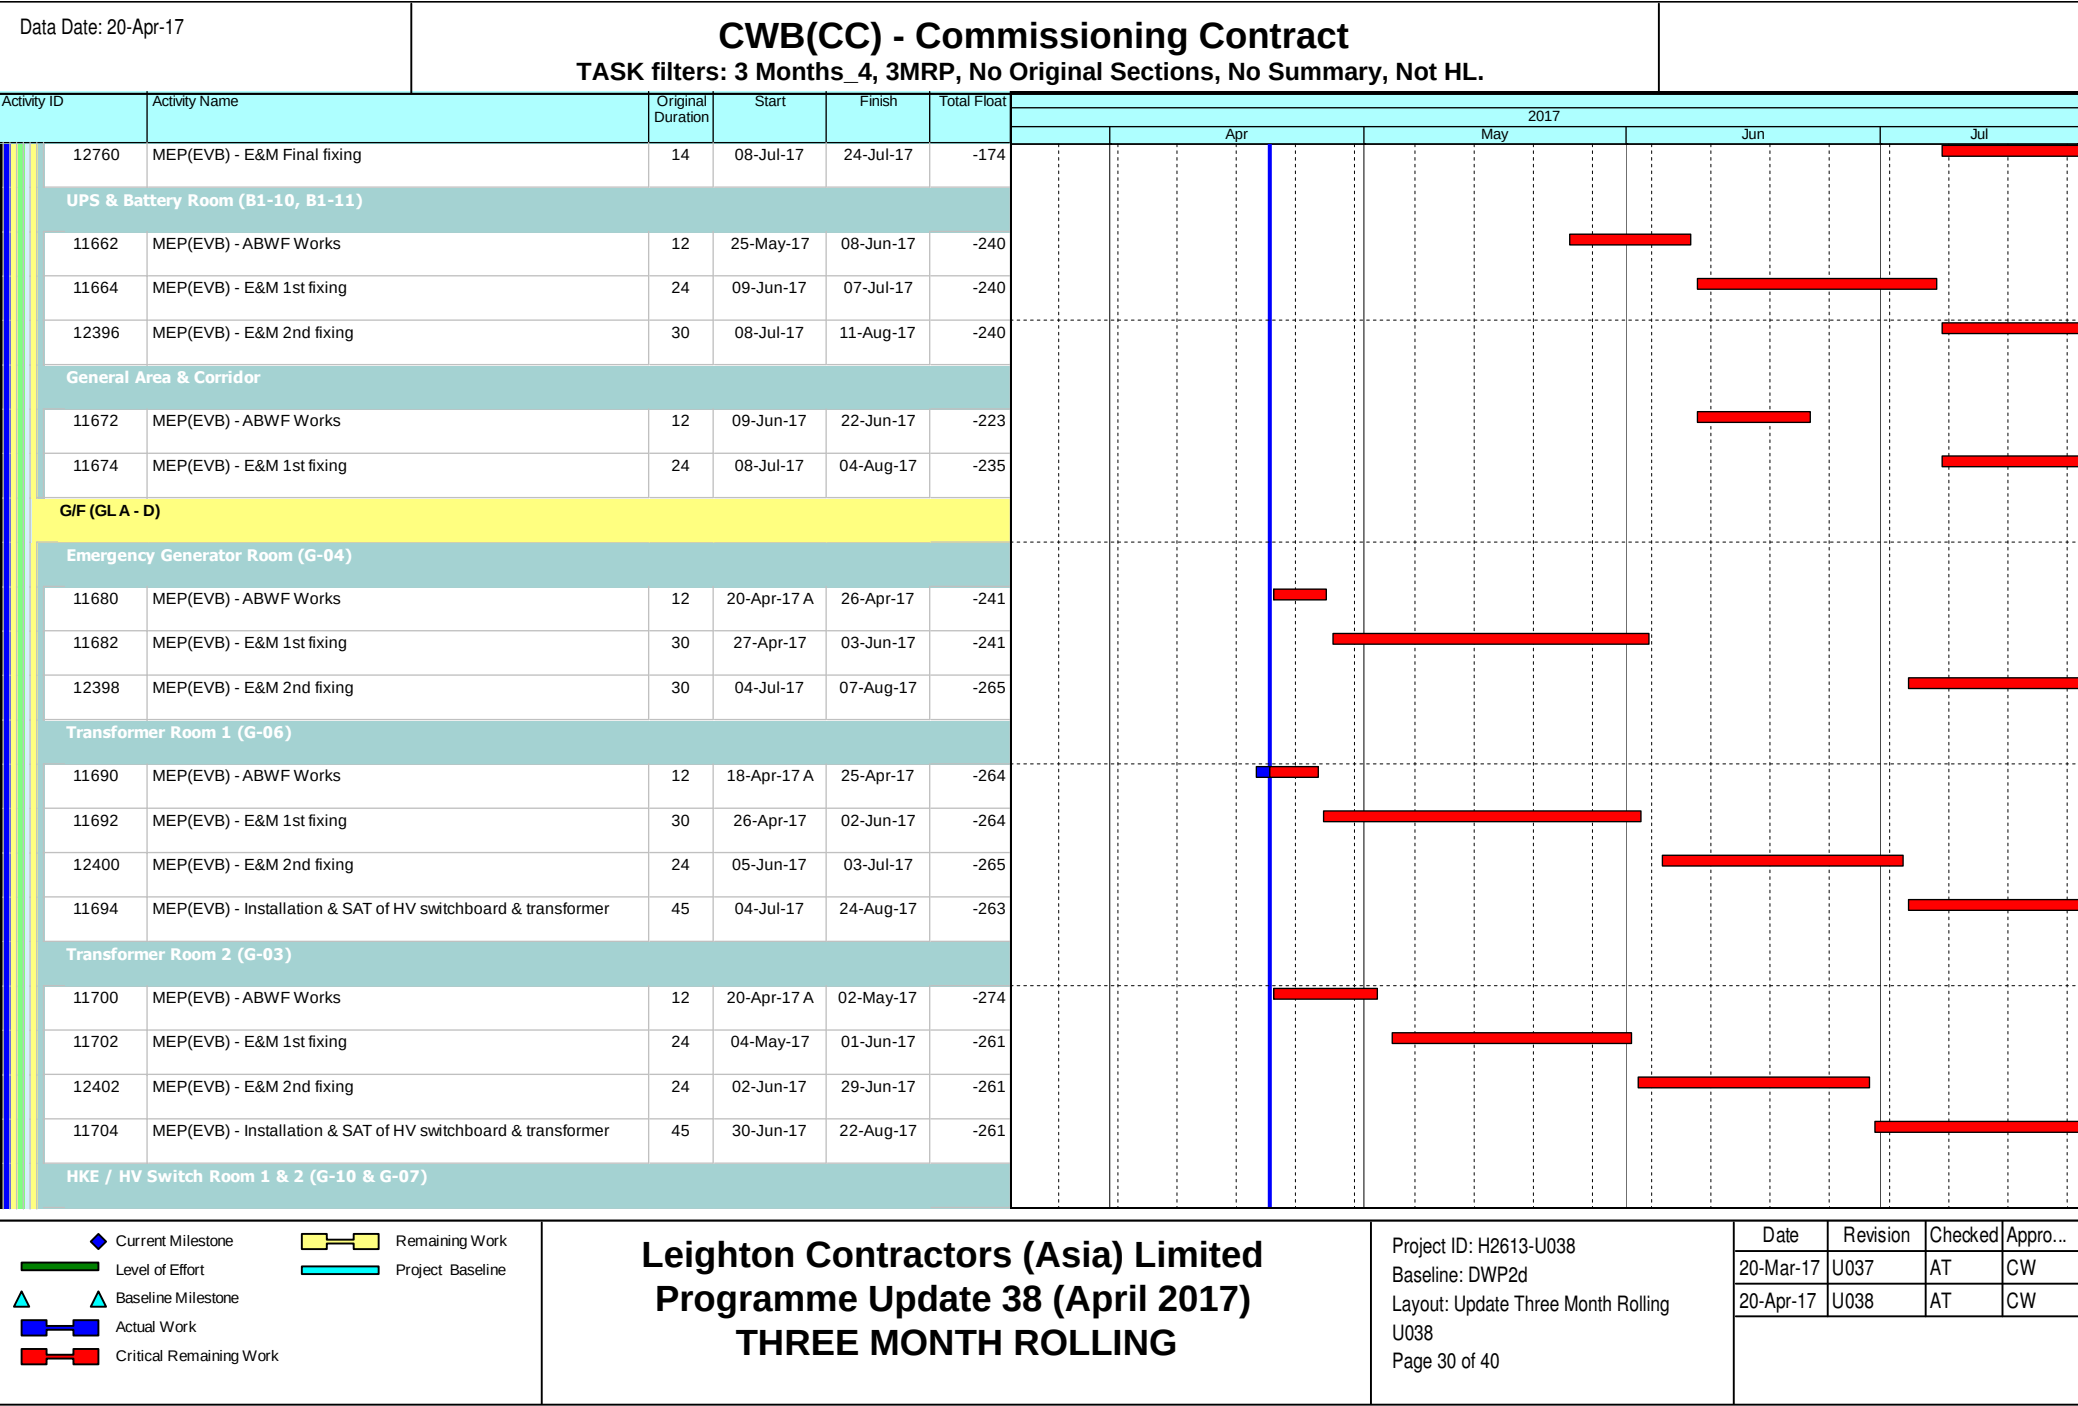


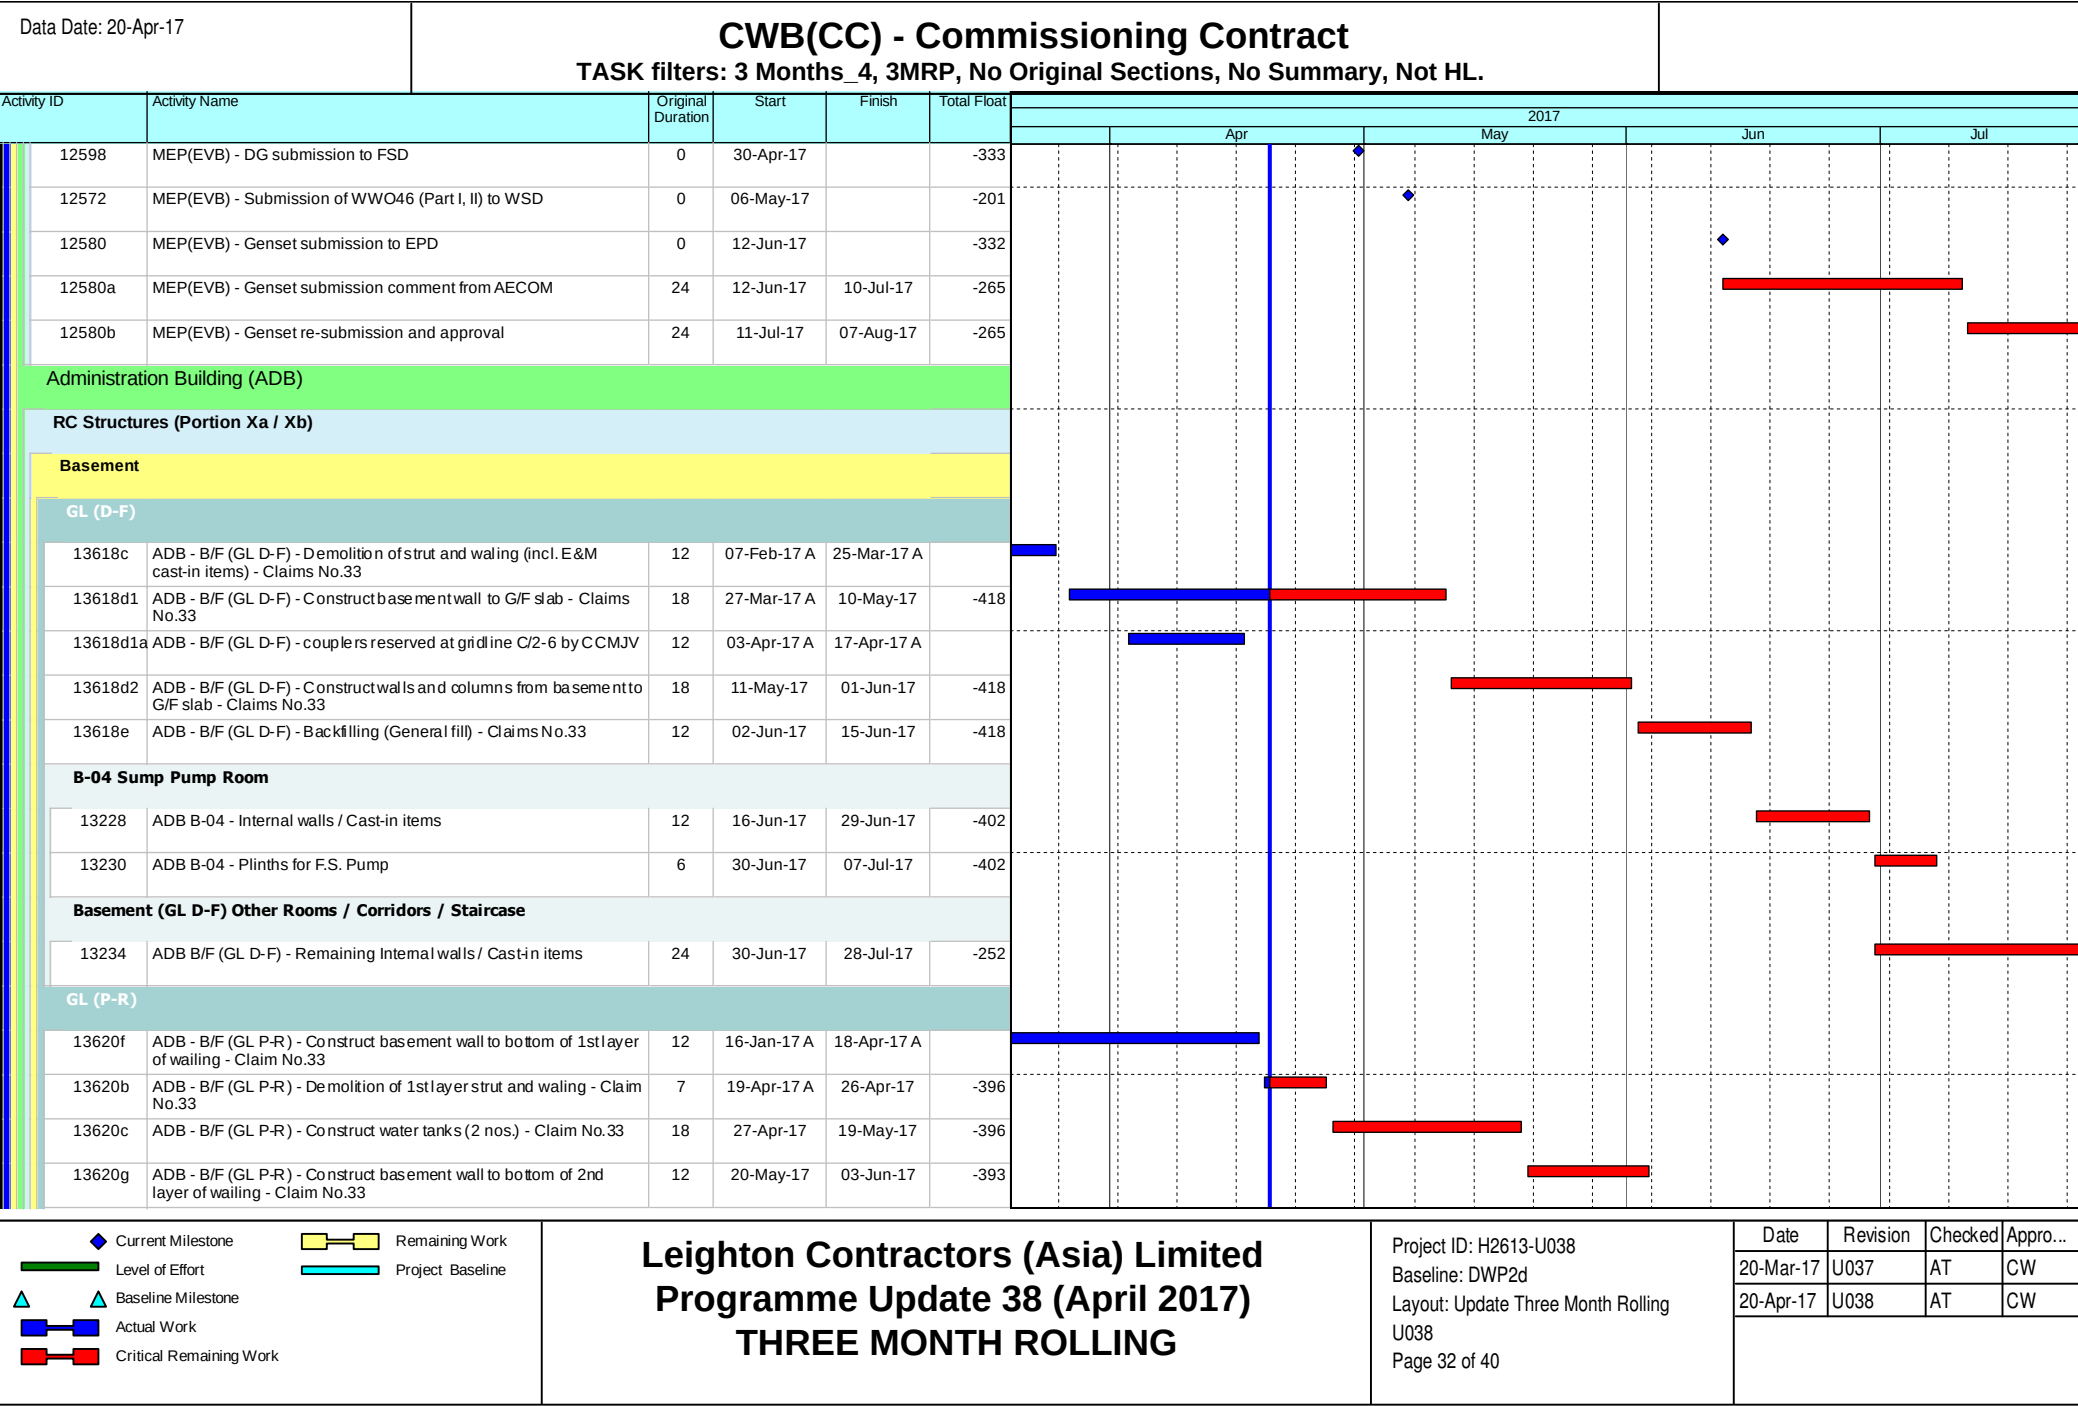


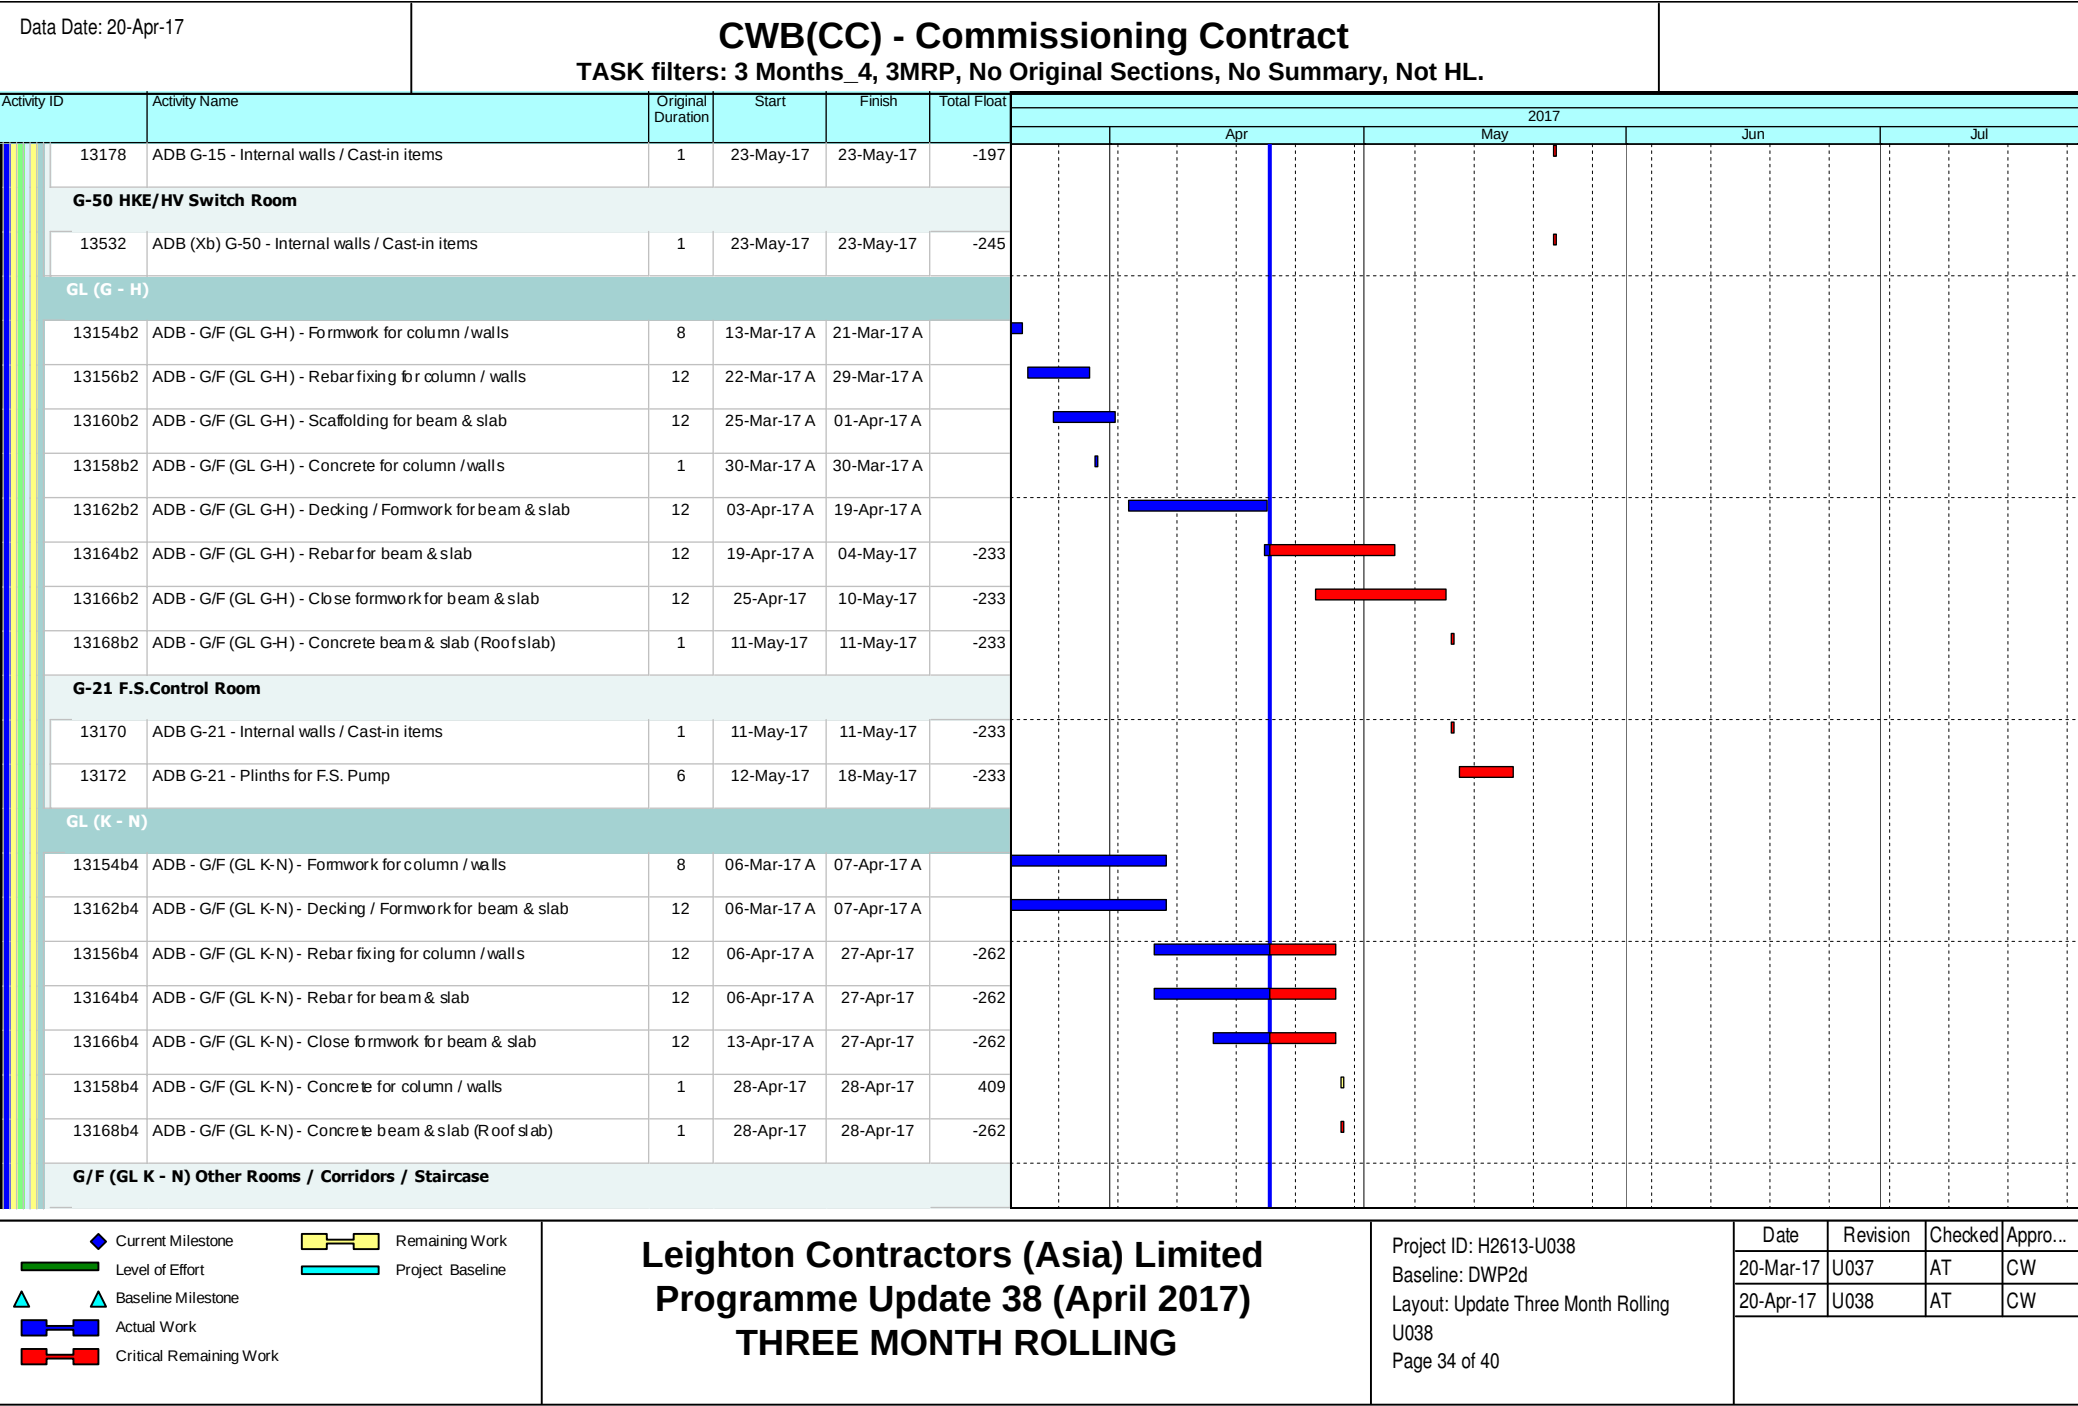


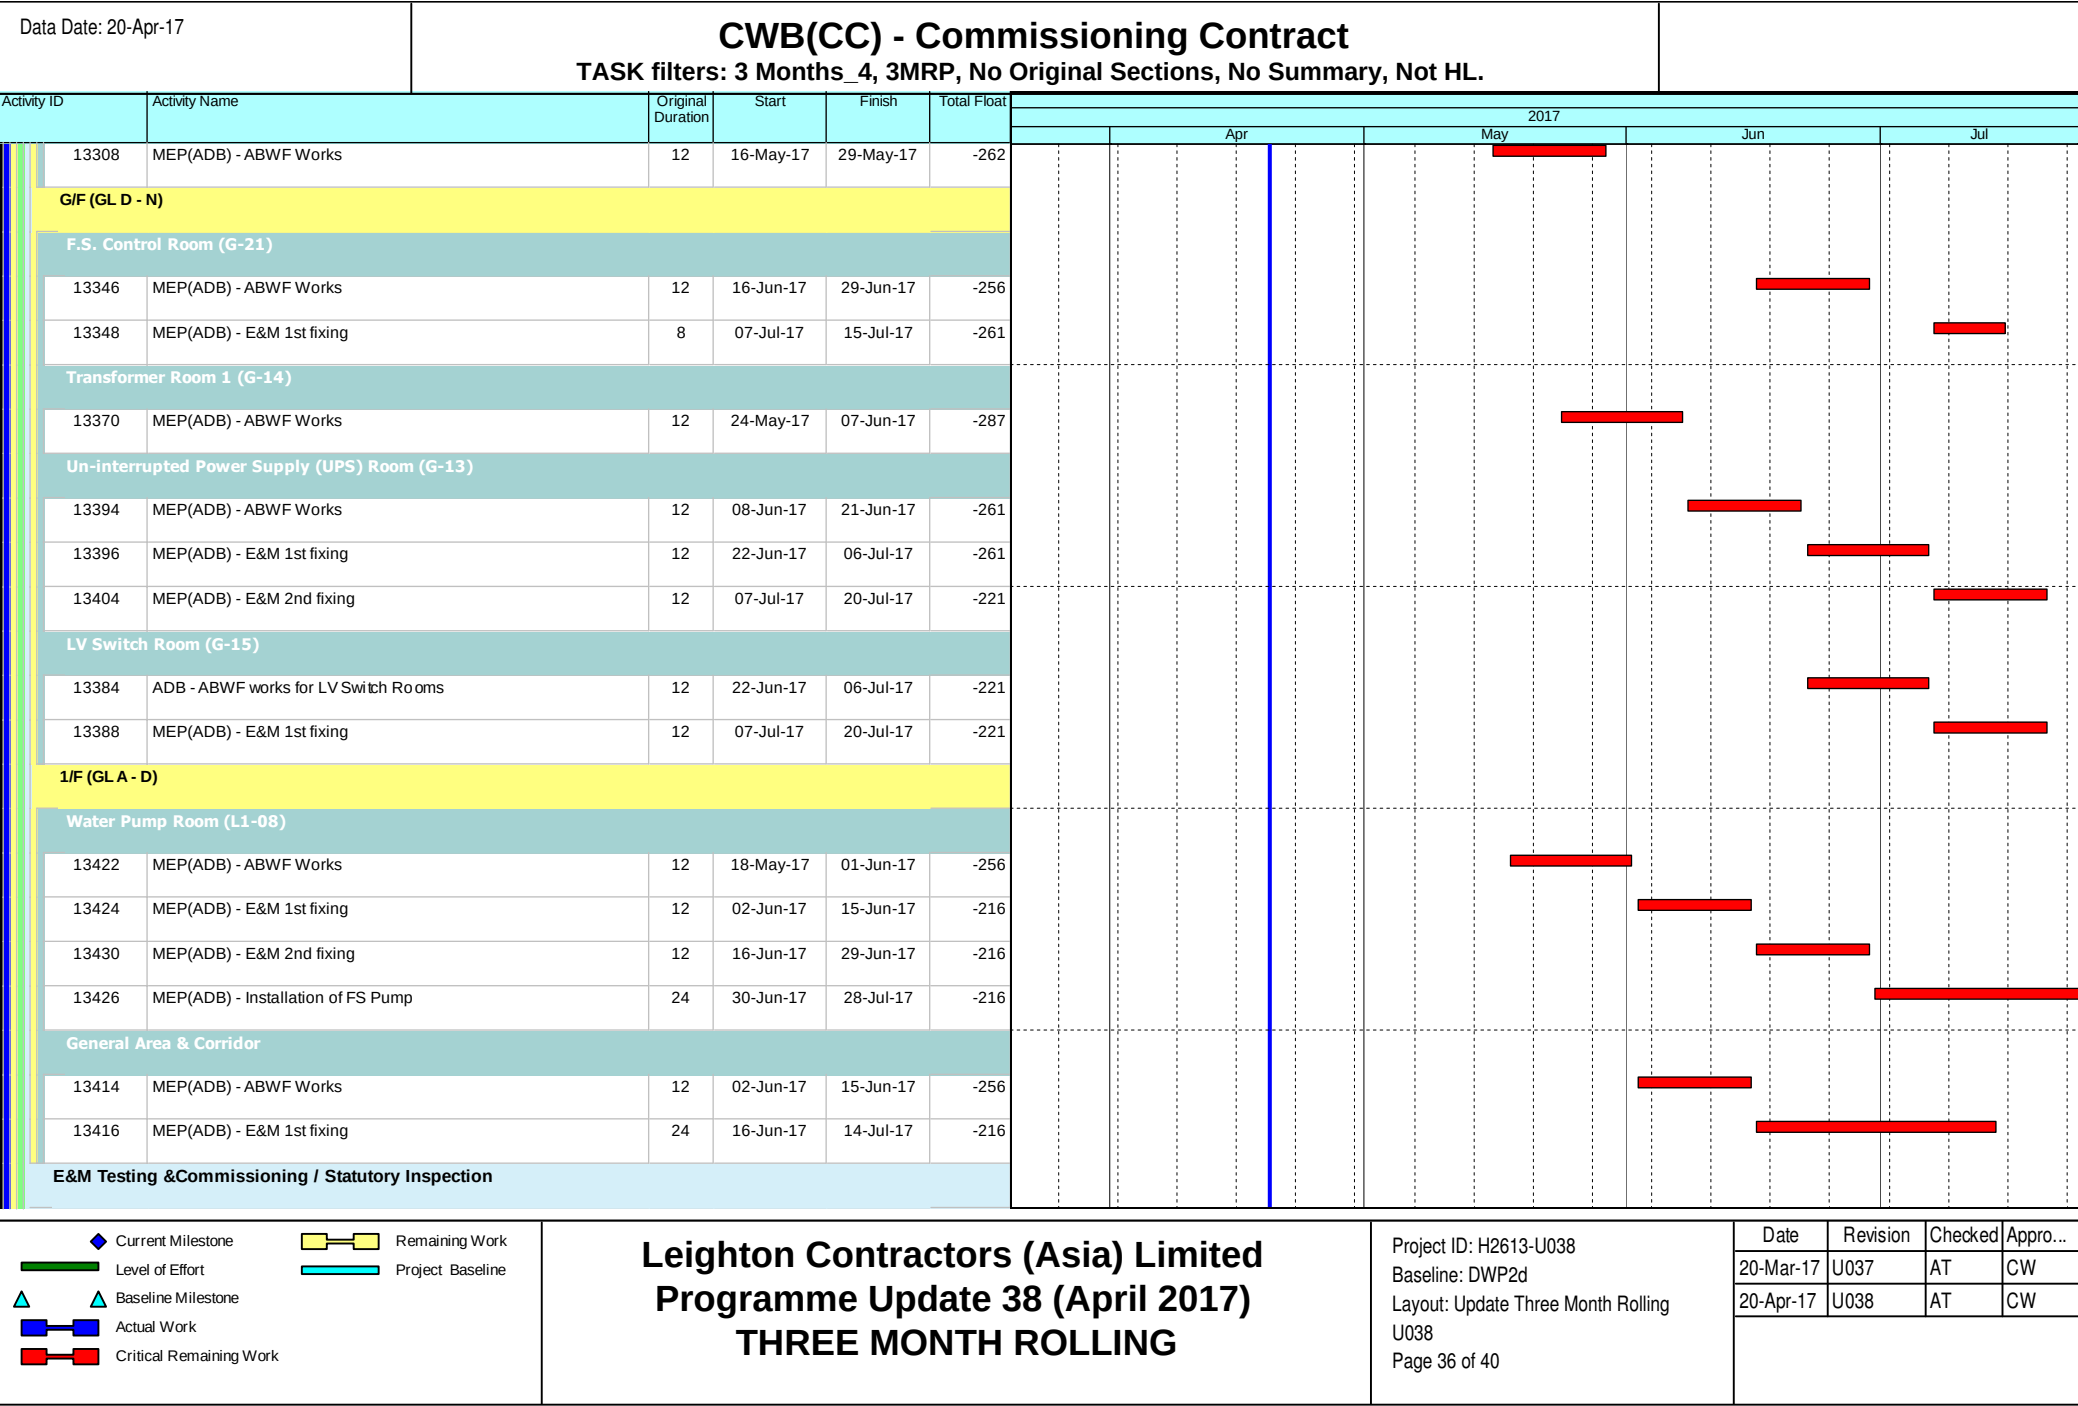














Data Date: 20-Apr-17

CWB(CC) - Commissioning Contract

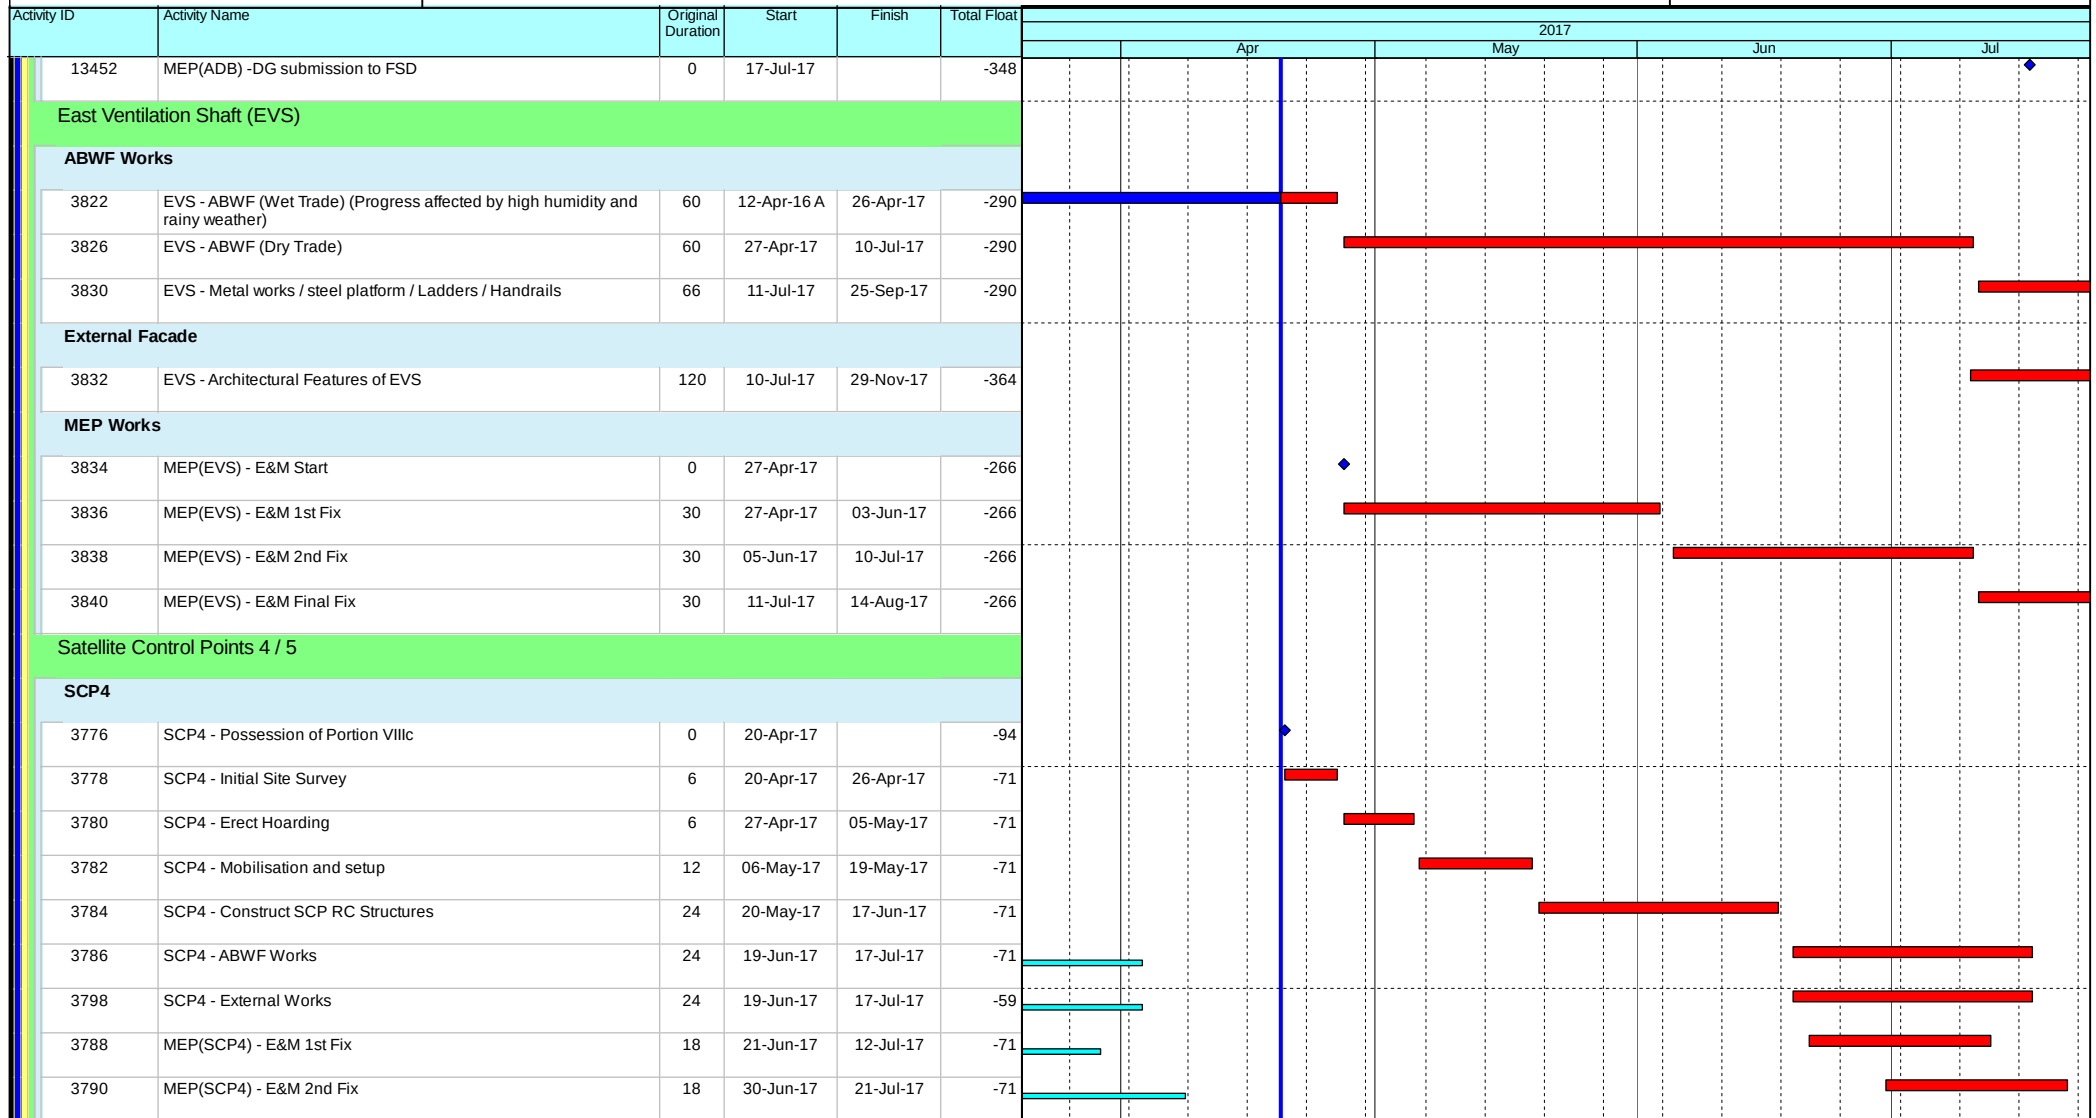TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.



Leighton Contractors (Asia) Limited Programme Update 38 (April 2017) THREE MONTH ROLLING

Project ID: H2613-U038
 Baseline: DWP2d
 Layout: Update Three Month Rolling
 U038
 Page 37 of 40

Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

Data Date: 20-Apr-17			CWB(CC) - Commissioning Contract TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																												
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2017																									
						Apr			May			Jun			Jul																
3824	SCP4 - Metal works / Glazing / Louver / Handrails	18	04-Jul-17	24-Jul-17	-65																										
3792	MEP(SCP4) - E&M Final Fix	18	11-Jul-17	31-Jul-17	-71																										
SCP5																															
3828	SCP5 - Mobilization for Area B	0	29-Apr-17		-241																										
3848	SCP5 - Initial Site Survey	6	29-Apr-17	08-May-17	-241																										
3852	SCP5 - Erect Hoarding	6	09-May-17	15-May-17	-241																										
3868	SCP5 - Mobilisation and setup	12	16-May-17	29-May-17	-241																										
3870a	SCP5 - Construct walls upto R/F - Falseworks & Formwork	5	31-May-17	05-Jun-17	-241																										
3870b	SCP5 - Construct walls upto R/F - Rebar fixing	3	06-Jun-17	08-Jun-17	-241																										
3870c	SCP5 - Construct walls upto R/F - Close formwork	5	09-Jun-17	14-Jun-17	-241																										
3870d	SCP5 - Construct beams & slab upto R/F - Scaffolding, falsework & formwork	7	15-Jun-17	22-Jun-17	-241																										
3870e	SCP5 - Construct beams & slab upto R/F - Rebar fixing	3	23-Jun-17	26-Jun-17	-241																										
3870f	SCP5 - Construct beams & slab upto R/F - Concreting	1	27-Jun-17	27-Jun-17	-241																										
3872	SCP5 - ABWF Works	24	28-Jun-17	26-Jul-17	-235																										
3886	SCP5 - External Works	30	28-Jun-17	02-Aug-17	-241																										
External Works																															
Area A/B																															
10288a3	Request for VO/instruction-TCSS equipment installation & cabling (Gantries FVMS1 /ADS01) (Ref: H27613-LJV-ME-LE-4022)	24	04-Oct-16 A	26-May-17	-162																										
10288f	C19 allow access at Area B	0	29-Apr-17*		-321																										
10288a1	Area A TCSS equipment installation and cabling (Gantry FVMS 1) - After C18 gantry installation complete	40	27-May-17	14-Jul-17	-162																										
10288a2	Area A TCSS equipment installation and cabling (Gantry ADS01) - Start date is tentative and to be confirmed	40	27-May-17	14-Jul-17	-162																										
Area B TCSS																															
Landscape Deck / Noise Enclosure (No TTA)																															
10288b1	Area B TCSS equipment installation and cabling (on IEC's Westbound)	120	29-Apr-17	20-Sep-17	-168																										
Current Milestone Level of Effort Baseline Milestone Actual Work Critical Remaining Work Remaining Work Project Baseline						Leighton Contractors (Asia) Limited Programme Update 38 (April 2017) THREE MONTH ROLLING						Project ID: H2613-U038 Baseline: DWP2d Layout: Update Three Month Rolling U038 Page 38 of 40				<table><tr><td>Date</td><td>Revision</td><td>Checked</td><td>Appro...</td></tr><tr><td>20-Mar-17</td><td>U037</td><td>AT</td><td>CW</td></tr><tr><td>20-Apr-17</td><td>U038</td><td>AT</td><td>CW</td></tr></table>				Date	Revision	Checked	Appro...	20-Mar-17	U037	AT	CW	20-Apr-17	U038	AT	CW
Date	Revision	Checked	Appro...																												
20-Mar-17	U037	AT	CW																												
20-Apr-17	U038	AT	CW																												

Data Date: 20-Apr-17

CWB(CC) - Commissioning Contract
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

CWB(CC) - Commissioning Contract
TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.

[illegible]

 Current Milestone
 Level of Effort
 Baseline Milestone
 Actual Work
 Critical Remaining Work

 Remaining Work
 Project Baseline

Leighton Contractors (Asia) Limited

Programme Update 38 (April 2017)

THREE MONTH ROLLING


Project ID: H2613-U038

Baseline: DWP2d


Layout: Update Three Month Rolling U038


Page 40 of 40


Date	Revision	Checked	Appro...
20-Mar-17	U037	AT	CW
20-Apr-17	U038	AT	CW

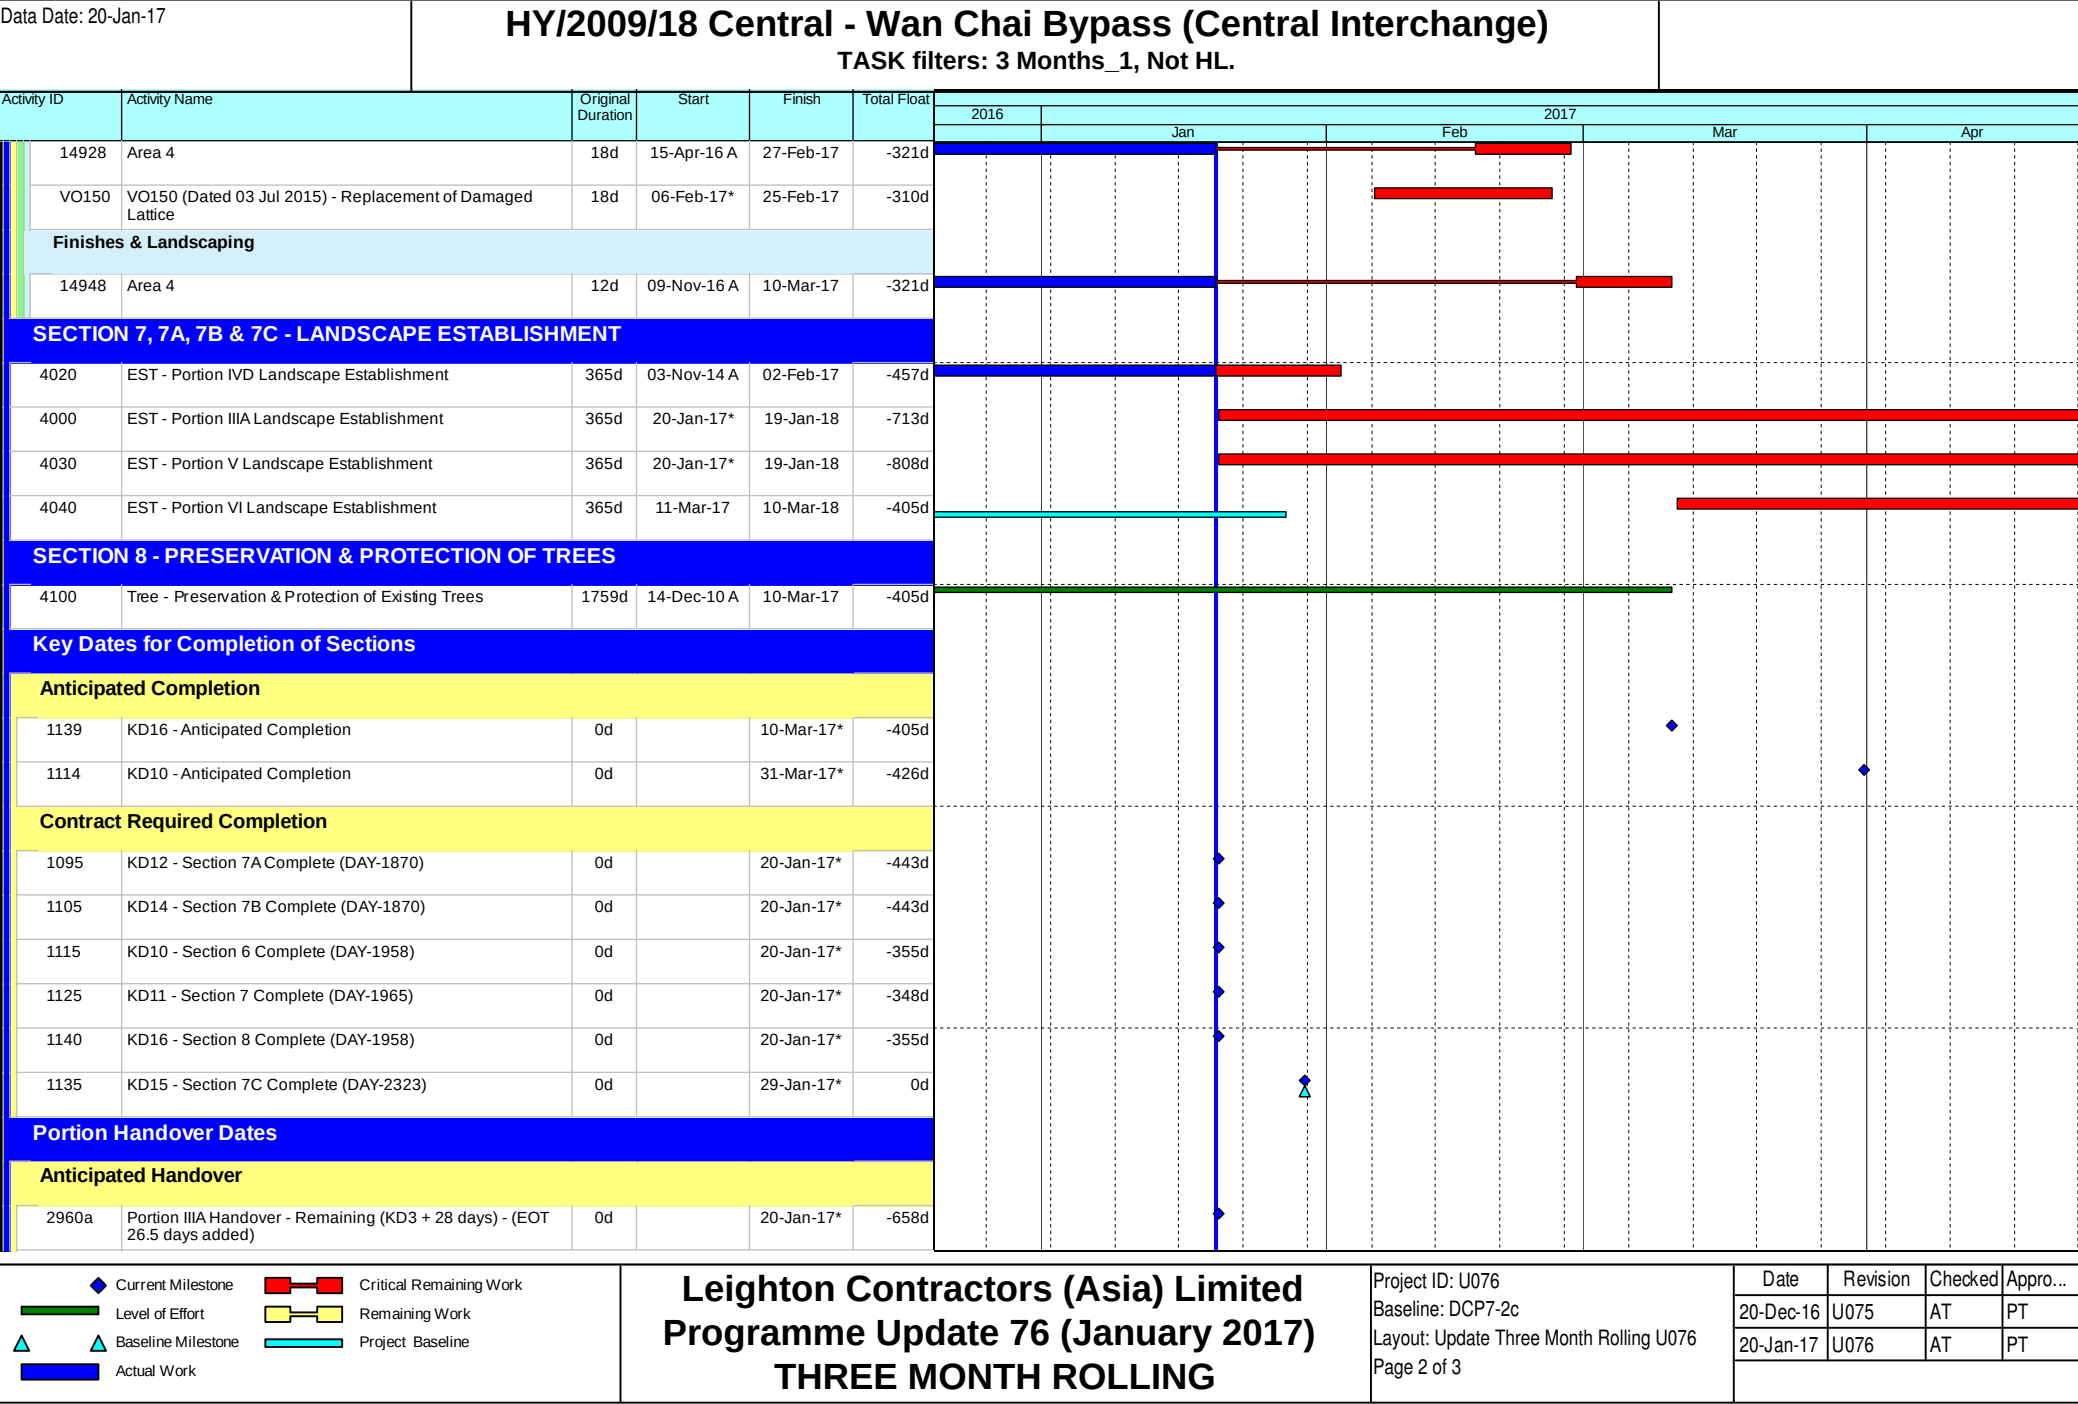

Data Date: 20-Jan-17		HY/2009/18 Central - Wan Chai Bypass (Central Interchange)															
		TASK filters: 3 Months_1, Not HL.															
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float												
						2016	2017										
							Jan		Feb		Mar		Apr				
Contract Required Handover																	
3096	Portion VI Handover (KD10 + 28 days)	0d		20-Jan-17*	-327d												



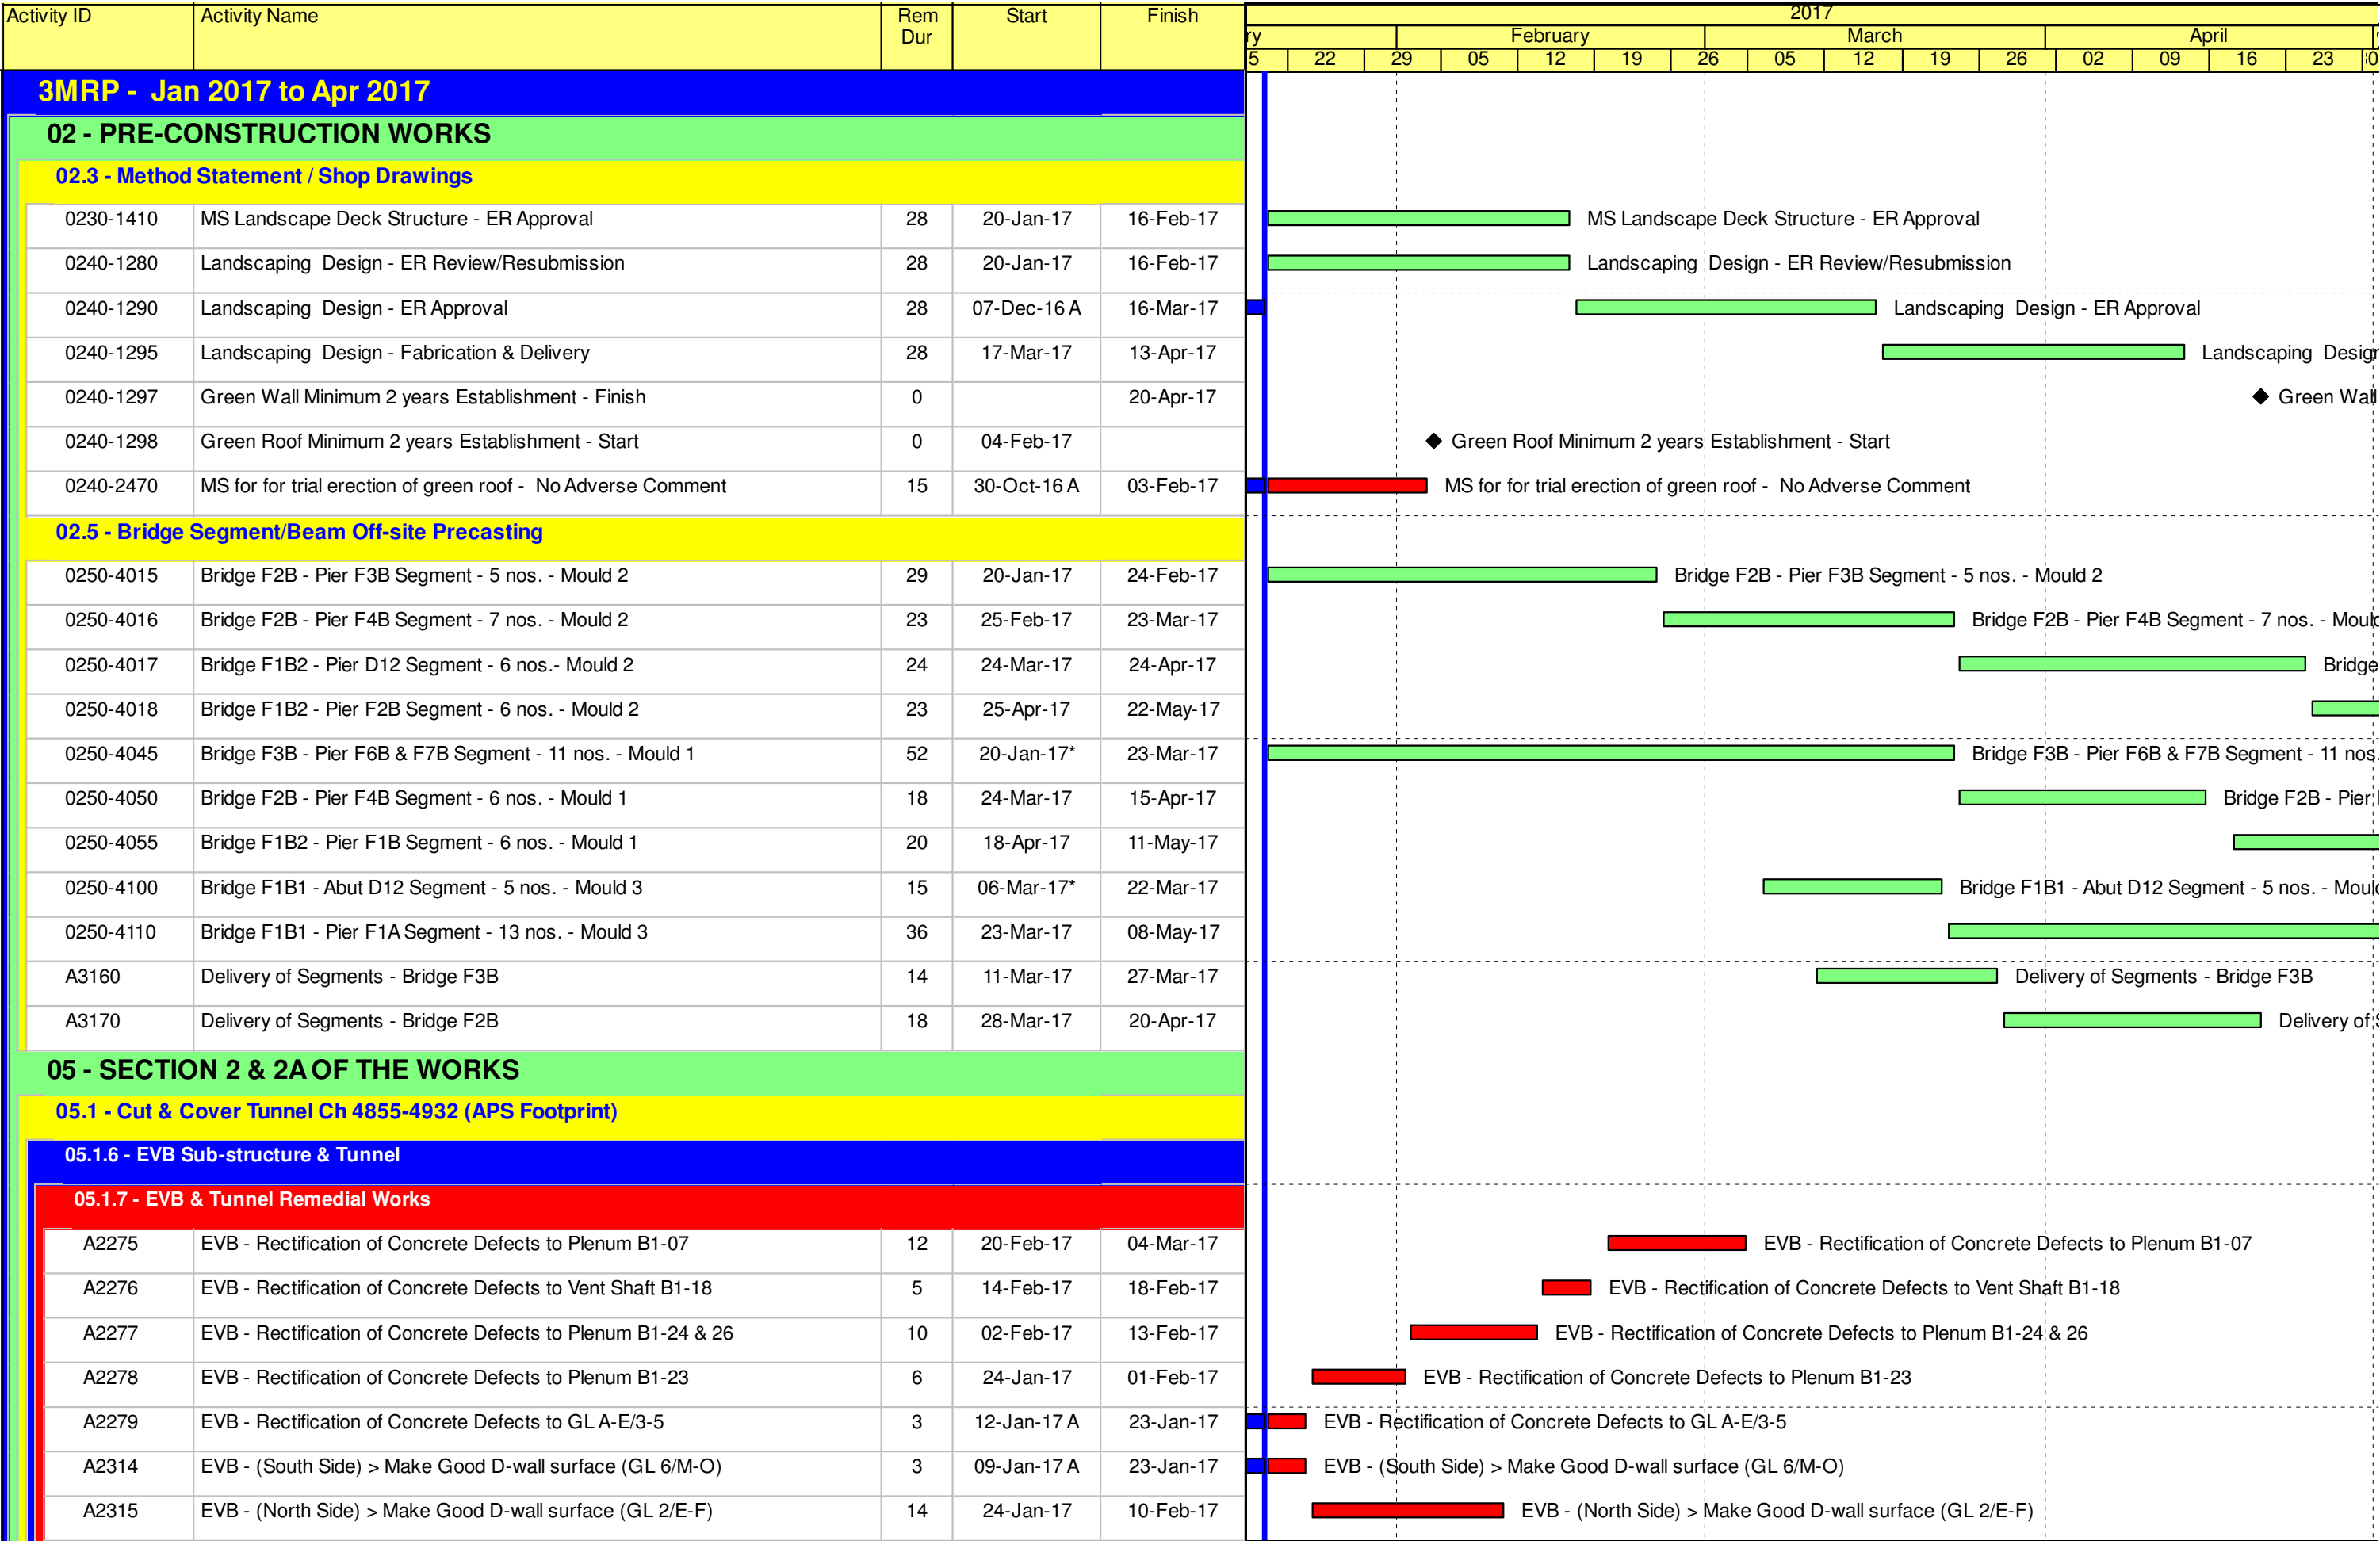

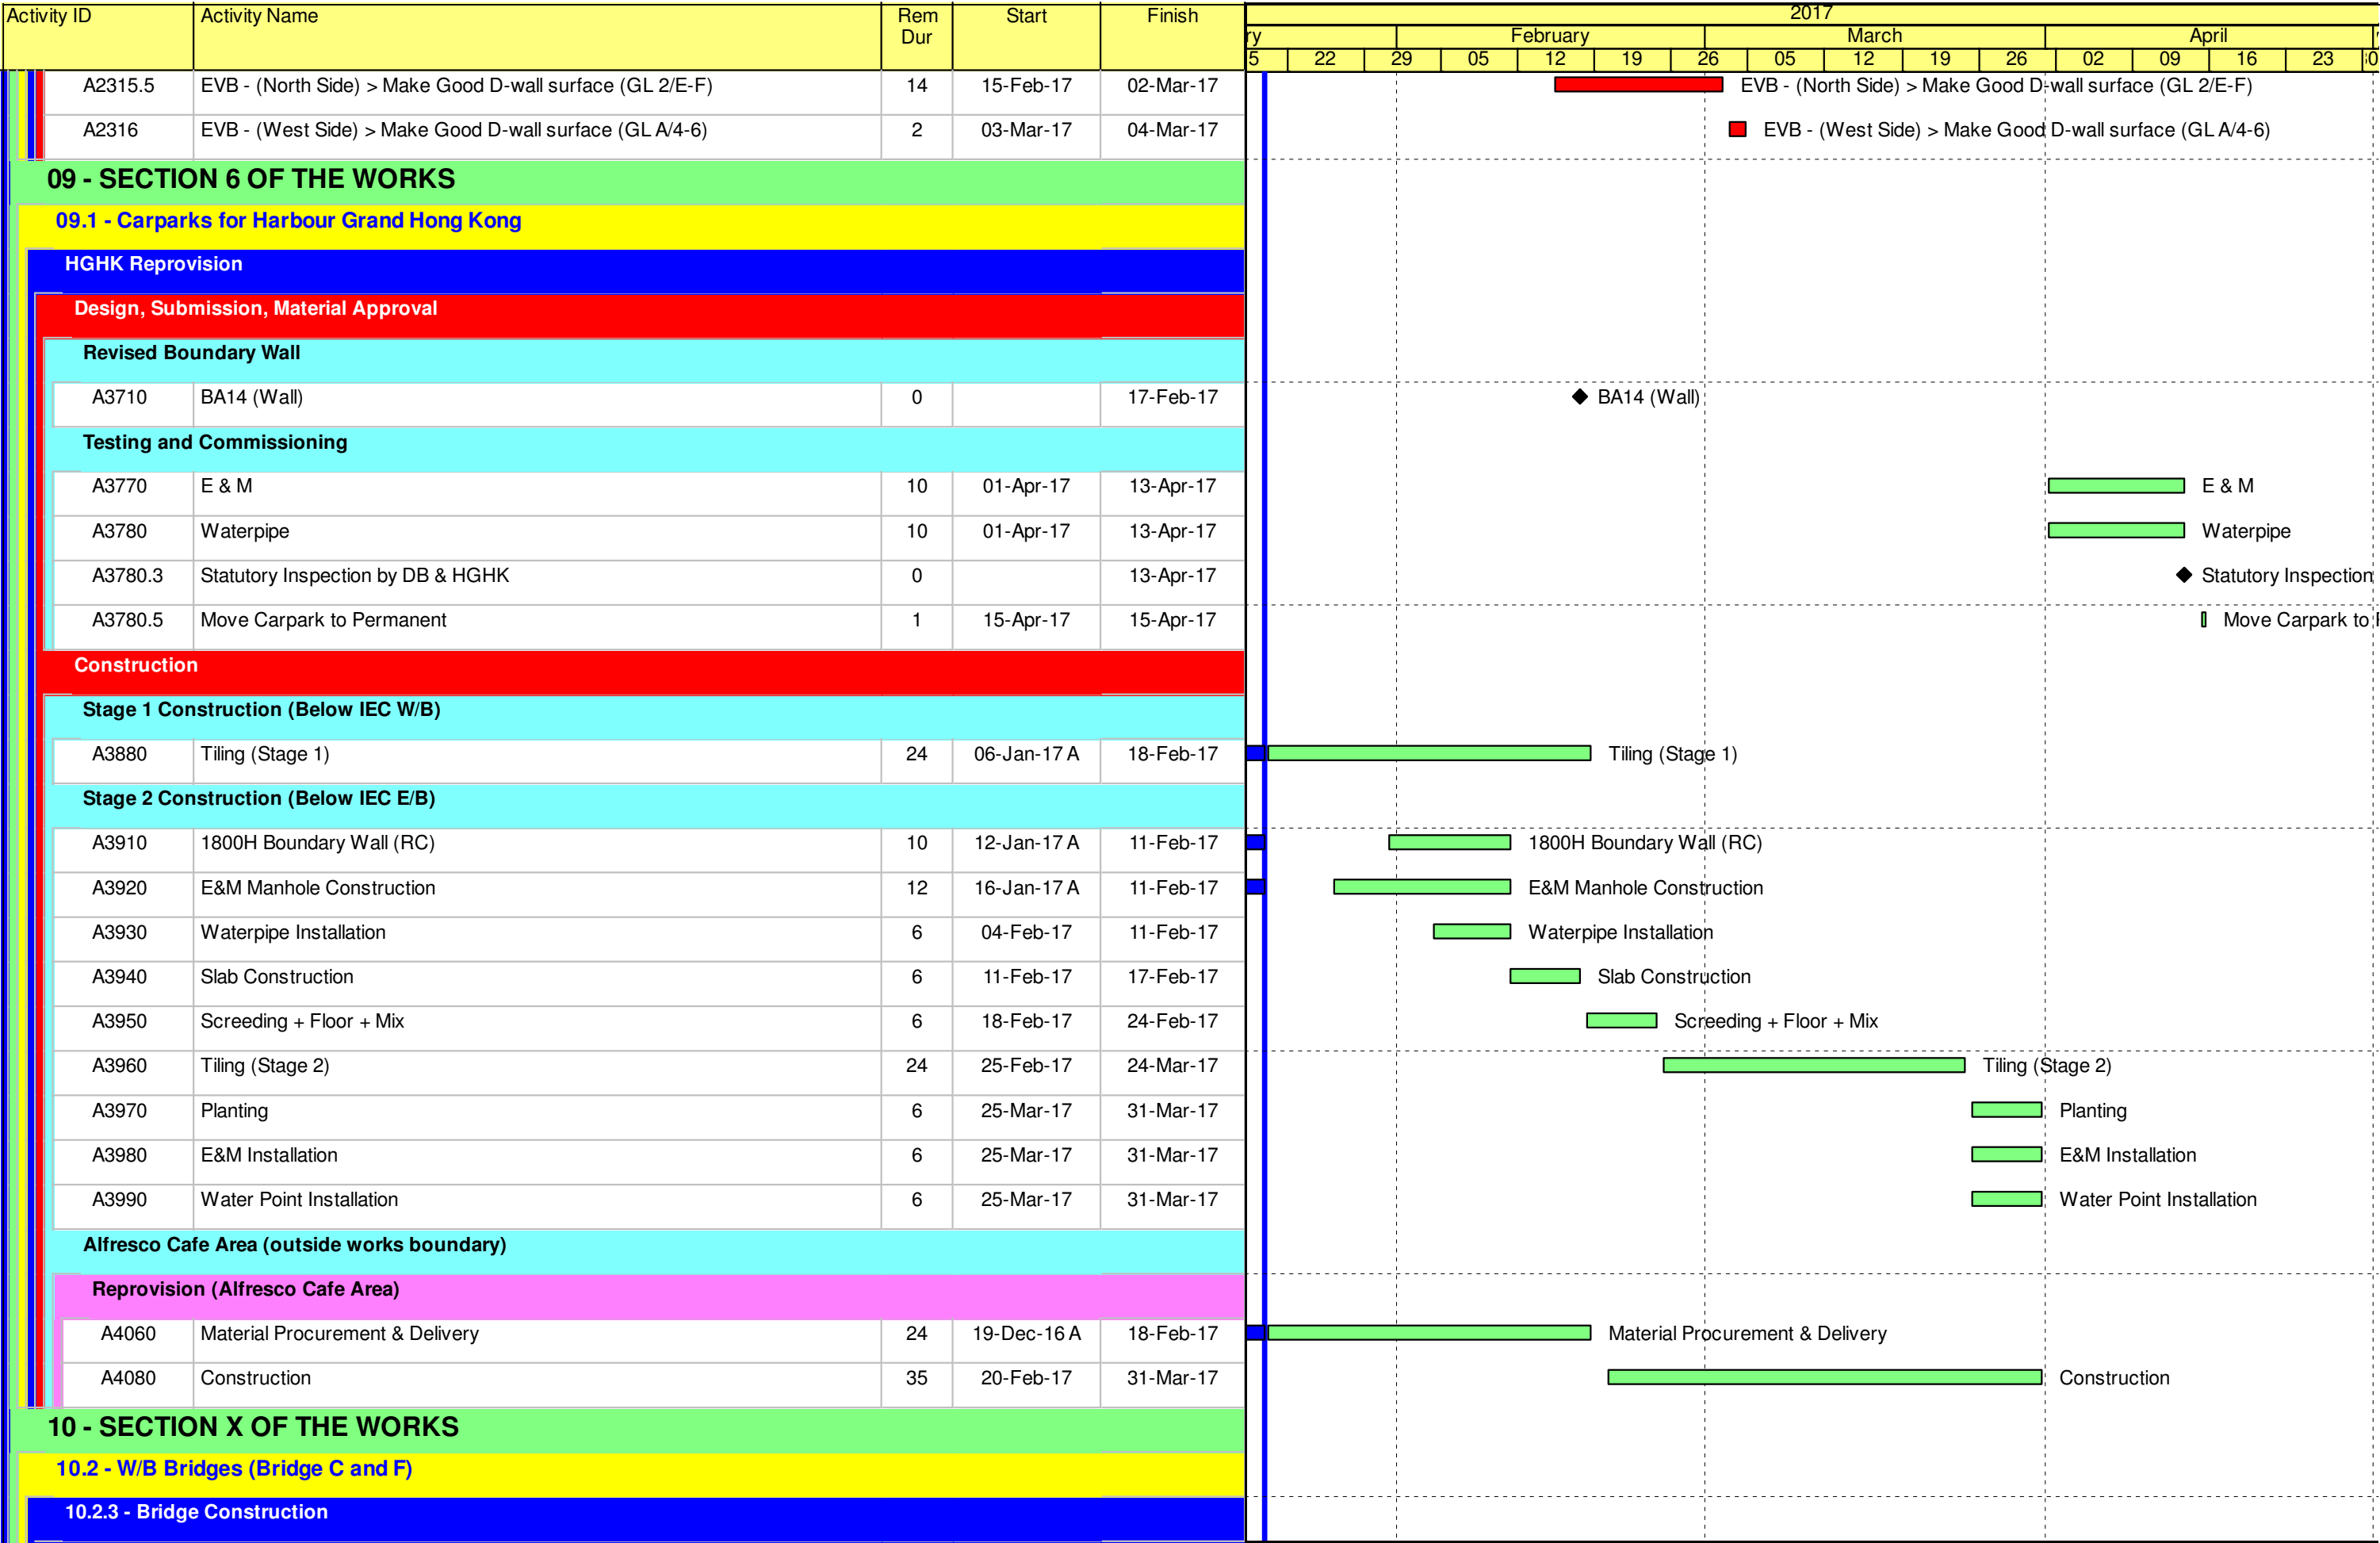

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																			
					January					February					March					April				
					5	12	19	26	31	5	12	19	26	31	5	12	19	26	31	5	12	19	26	31
Bridge C1	Outstanding Works Between Bridge C1 & E																							
	A4530	Pier 17 to 18 - Steel Mould Erection	2	20-Jan-17	21-Jan-17	■ Pier 17 to 18 - Steel Mould Erection																		
	A4550	Pier 17 to 18 - Concreting	1	23-Jan-17	23-Jan-17	■ Pier 17 to 18 - Concreting																		
	A4570	Pier 16 to 17 - Forwork Erection	2	20-Jan-17	21-Jan-17	■ Pier 16 to 17 - Forwork Erection																		
	A4590	Pier 16 to 17 - Rebar Bending	2	20-Jan-17	21-Jan-17	■ Pier 16 to 17 - Rebar Bending																		
	A4610	Pier 16 to 17 - Rebar Fixing	2	23-Jan-17	24-Jan-17	■ Pier 16 to 17 - Rebar Fixing																		
	A4630	Pier 16 to 17 - Steel Mould Erection	2	25-Jan-17	26-Jan-17	■ Pier 16 to 17 - Steel Mould Erection																		
	A4650	Pier 16 to 17 - Concreting	1	27-Jan-17	27-Jan-17	■ Pier 16 to 17 - Concreting																		
	A4670	Pier 15 to 16 - Forwork Erection	2	24-Jan-17	25-Jan-17	■ Pier 15 to 16 - Forwork Erection																		
	A4690	Pier 15 to 16 - Rebar Bending	2	24-Jan-17	25-Jan-17	■ Pier 15 to 16 - Rebar Bending																		
	A4710	Pier 15 to 16 - Rebar Fixing	2	26-Jan-17	27-Jan-17	■ Pier 15 to 16 - Rebar Fixing																		
	A4730	Pier 15 to 16 - Steel Mould Erection	2	31-Jan-17	01-Feb-17	■ Pier 15 to 16 - Steel Mould Erection																		
	A4750	Pier 15 to 16 - Concreting	1	02-Feb-17	02-Feb-17	■ Pier 15 to 16 - Concreting																		
	A4770	Temp Lighting (2 Nos)	2	07-Feb-17	08-Feb-17	■ Temp Lighting (2 Nos)																		
	A4790	Noise Barrier Const. Pier E1 to D1	12	20-Jan-17	04-Feb-17	■ Noise Barrier Const. Pier E1 to D1																		
	A4810	Noise Barrier Const. Pier 18 to 19	13	06-Feb-17	20-Feb-17	■ Noise Barrier Const. Pier 18 to 19																		
	A4830	Noise Barrier Const. Pier 17 to 18	12	21-Feb-17	06-Mar-17	■ Noise Barrier Const. Pier 17 to 18																		
	A4850	Paving & Road Marking	2	07-Mar-17	08-Mar-17	■ Paving & Road Marking																		
10.3 - Middle Bridge (Bridge F)																								
10.3.1 - Pier Construction																								
Pier F1B2 to F4B																								
1031-1440	Existing P39/F4B Prepare C.J.	7	04-Apr-17	12-Apr-17	■ Existing P39/F4B Prepare C.J.																			
1031-1460	Existing P39/F4B Construct Pier/Column	14	13-Apr-17	02-May-17	■ Existing P39/F4B Construct Pier/Column																			
Pier F5B to F8B																								
1031-1520	Existing P40/F5B Prepare C.J.	6	21-Mar-17	27-Mar-17	■ Existing P40/F5B Prepare C.J.																			
1031-1540	Existing P40/F5B Construct Pier/Column	14	28-Mar-17	13-Apr-17	■ Existing P40/F5B Construct Pier/Column																			
1031-1600	Existing P41/F6B Prepare C.J.	6	07-Mar-17	13-Mar-17	■ Existing P41/F6B Prepare C.J.																			
1031-1620	Existing P41/F6B Construct Pier/Column	14	14-Mar-17	29-Mar-17	■ Existing P41/F6B Construct Pier/Column																			
1031-1640	Existing P41/F6B Construct Crosshead	18	30-Mar-17	22-Apr-17	■ Existing P41/F6B Construct Crosshead																			
1031-1680	Existing P42/F7B Prepare C.J.	6	21-Feb-17	27-Feb-17	■ Existing P42/F7B Prepare C.J.																			
1031-1700	Existing P42/F7B Construct Pier/Column	14	28-Feb-17	15-Mar-17	■ Existing P42/F7B Construct Pier/Column																			
1031-1720	Existing P42/F7B Construct Crosshead	18	16-Mar-17	06-Apr-17	■ Existing P42/F7B Construct Crosshead																			

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

[illegible]

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																
					January			February				March				April					
					5	22	29	05	12	19	26	05	12	19	26	02	09	16	23	30	
10.6 - Section 10.6 - Pumping Test	1061-5100	Pumping Test	9	14-Mar-17	23-Mar-17																
	1061-5120	Complete Pump Test	0		23-Mar-17																
	1061-5140	Ch 5285 - 5331 > Excav from Ex. Lvl down to 2.5mPD (Ch 5285 - 5331 w/ open cut)	18	15-Aug-16 A	11-Feb-17																
	1061-5160	Ch 5234 - 5285 > Excav from Ex. Lvl down to 2.5mPD	20	13-Feb-17	07-Mar-17																
	1061-5180	Ch 5234 - 5285 > Install 1st Layer of Strut & Waling	9	11-Mar-17	21-Mar-17																
	1061-5200	Ch 5234 - 5285 > Excav from 2.5mPD to 1m Below 2nd Layer of Struts	16	24-Mar-17	12-Apr-17																
	1061-5220	Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling	9	13-Apr-17	25-Apr-17																
	1061-5240	Ch 5234 - 5285 > Excav to FEL	13	26-Apr-17	11-May-17																
Structure Works																					
1061-5260	Bay 1 - Ch 5322 - 5331 > Base Slab - Blinding Layer	1	13-Apr-17	13-Apr-17																	
1061-5280	Bay 1 - Ch 5322 - 5331 > Base Slab - Water Proofing Membrane	2	15-Apr-17	18-Apr-17																	
1061-5300	Bay 1 - Ch 5322 - 5331 > Base Slab - Rebar Fixing	5	19-Apr-17	24-Apr-17																	
10.7 - Section X - Miscellaneous Works																					
10.7.3 - Open Area																					
1073-1010	Open Area - Pedestrian Parapet -Ch570.40 to Ch540.00	14	17-Feb-17*	04-Mar-17																	
1073-1010.3	Open Area - Pedestrian Parapet - Ch540.00 to Ch520.00	14	06-Mar-17	21-Mar-17																	
1073-1010.5	Open Area - Pedestrian Parapet - Ch0.00 - Ch40.00	18	22-Mar-17	12-Apr-17																	
1073-1010.7	Open Area - Pedestrian Parapet - Ch40.00 - 80.00	18	13-Apr-17	06-May-17																	
11 - SECTION 11 OF THE WORKS																					
11.1 - Portion XIIA - Stage 1																					
11.1.1 - Along Watson Road - Waterwork & Roadworks (Portion XIIA)																					
1110-2820	Permanent Cul-de Sac - Constr. of drainage	25	06-Feb-17*	06-Mar-17																	
1110-2830	Permanent Cul-de Sac - Constr. of watermains	25	17-Feb-17	17-Mar-17																	
1110-2840	Permanent Cul-de Sac - Constr. of public lighting & telecom (conduits & drawpits)	25	01-Mar-17	29-Mar-17																	
1110-2850	Permanent Cul-de Sac - Constr. of (kerbs & pavements)	25	30-Mar-17	02-May-17																	
11.1.3 - Along Tsing Fung St. - TCSS cable ducting (Portion XIIA)																					
1110-2930	TCSS cable ducting along Tsing Fung St	36	06-Mar-17*	19-Apr-17																	

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work


Critical Remaining Work

Milestone

Milestone

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
									May				June				July			
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
3MRP - Apr 2017 to Jul 2017																				
02 - PRE-CONSTRUCTION WORKS																				
02.3 - Method Statement / Shop Drawings																				
0230-1410	MS Landscape Deck Structure - ER Approval	28	20-Apr-17	17-May-17	MS Landscape Deck Structure - ER Approval															
0240-1280	Landscaping Design - ER Review/Resubmission	28	20-Apr-17	17-May-17	Landscaping Design - ER Review/Resubmission															
0240-1290	Landscaping Design - ER Approval	28	07-Dec-16 A	14-Jun-17	Landscaping Design - ER Approval															
0240-1295	Landscaping Design - Fabrication & Delivery	28	15-Jun-17	12-Jul-17	Landscaping Design -															
0240-1298	Green Roof Minimum 2 years Establishment - Start	0	05-May-17		◆ Green Roof Minimum 2 years Establishment - Start															
0240-2470	MS for for trial erection of green roof - No Adverse Comment	15	30-Oct-16 A	04-May-17	MS for for trial erection of green roof - No Adverse Comment															
02.5 - Bridge Segment/Beam Off-site Precasting																				
0250-4017	Bridge F1B2 - Pier D12 Segment - 6 nos.- Mould 2	4	24-Mar-17 A	24-Apr-17	Bridge F1B2 - Pier D12 Segment - 6 nos.- Mould 2															
0250-4018	Bridge F1B2 - Pier F2B Segment - 6 nos. - Mould 2	23	25-Apr-17	22-May-17	Bridge F1B2 - Pier F2B Segment - 6 nos. - Mould 2															
0250-4019	Bridge F1B2 - Pier F3B Segment - 5 nos. - Mould 2	14	23-May-17	08-Jun-17	Bridge F1B2 - Pier F3B Segment - 5 nos. - Mould 2															
0250-4055	Bridge F1B2 - Pier F1B Segment - 6 nos. - Mould 1	18	18-Apr-17 A	11-May-17	Bridge F1B2 - Pier F1B Segment - 6 nos. - Mould 1															
0250-4057	Bridge F1B2 - Abut D12 Segment - 6 nos. - Mould 1	18	12-May-17	02-Jun-17	Bridge F1B2 - Abut D12 Segment - 6 nos. - Mould 1															
0250-4059	Bridge F1B2 - Pier F2B Segment - 5 nos. - Mould 1	13	03-Jun-17	17-Jun-17	Bridge F1B2 - Pier F2B Segment - 5 nos. - Mould 1															
0250-4110	Bridge F1B1 - Pier F1A Segment - 13 nos. - Mould 3	15	23-Mar-17 A	08-May-17	Bridge F1B1 - Pier F1A Segment - 13 nos. - Mould 3															
0250-4115	Bridge F1B1 - Pier F2A Segment - 11nos. - Mould 3	32	09-May-17	15-Jun-17	Bridge F1B1 - Pier F2A Segment - 11nos. - Mould 3															
0250-4120	Bridge F1B1 - Pier F3A Segment - 6 nos. - Mould 3	17	16-Jun-17	06-Jul-17	Bridge F1B1 - Pier F3A Segment															
A3170	Delivery of Segments - Bridge F2B	3	28-Mar-17 A	22-Apr-17	Delivery of Segments - Bridge F2B															
A3180	Delivery of Segments - Bridge F1B2	18	01-Jun-17	21-Jun-17	Delivery of Segments - Bridge F1B2															
A3190	Delivery of Segments - Bridge F1B1	18	16-Jun-17	07-Jul-17	Delivery of Segments - Bridge															
03 - PRELIMINARY WORKS																				
03.3 - Interface Works																				
FEHD Permanent Depot																				
0330-1020	Breaking-up Slabs for Pole Installations (25Nos)	13	25-Apr-17	10-May-17	Breaking-up Slabs for Pole Installations (25Nos)															
0330-1023	Drilling & Base Plate Installation (M25 - 104Nos)	21	27-Apr-17	22-May-17	Drilling & Base Plate Installation (M25 - 104Nos)															
0330-1025	Installation of Pole (25Nos)	13	11-May-17	25-May-17	Installation of Pole (25Nos)															
0330-1027	Installtion of Beams (77Nos)	26	12-May-17	12-Jun-17	Installtion of Beams (77Nos)															
0330-1029	Installation of Bondek (Soffit Formworks)	12	05-Jun-17	17-Jun-17	Installation of Bondek (Soffit Formworks)															
0330-1031	Rebar Fixing	7	12-Jun-17	19-Jun-17	Rebar Fixing															
0330-1033	Edges Formworks	2	17-Jun-17	19-Jun-17	Edges Formworks															
0330-1035	Concreting of Deck	3	20-Jun-17	22-Jun-17	Concreting of Deck															
0330-1037	Breaking Slab for Brace Footing Construction (3Nos)	9	25-Apr-17	05-May-17	Breaking Slab for Brace Footing Construction (3Nos)															
0330-1039	Excavation for Brace Footing	3	06-May-17	09-May-17	Excavation for Brace Footing															

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
									May				June				July			
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
0330-1043	Construction of Brace Footing	5	10-May-17	15-May-17																
0330-1047	Erection of Bracing Beam (3Nos)	3	16-May-17	18-May-17																
0330-1049	Touch-up Painting	12	22-May-17	05-Jun-17																
0330-1051	Waterproofing & Slab Reinstatement	7	19-May-17	26-May-17																
0330-1053	Breaking Slab & Excavate for Lamp Pole Footing	7	11-May-17	18-May-17																
0330-1055	Construction of Lamp Pole Footing (12Nos)	21	12-May-17	06-Jun-17																
0330-1057	Drilling for Lamp Pole at Existing Slab (8Nos Poles; M16-64Nos)	8	18-May-17	26-May-17																
0330-1059	Installation of Lamp Pole (total 20Nos)	14	23-May-17	08-Jun-17																
0330-1061	Breaking Existing Slab for Cross Road Ducting (Approx 300m)	18	24-May-17	14-Jun-17																
0330-1063	Laying Duct	5	15-Jun-17	20-Jun-17																
0330-1065	Cabling Works	9	21-Jun-17	30-Jun-17																
0330-1067	Slab Reinstatement	8	03-Jul-17	11-Jul-17																
0330-1069	Drilling for Post Anchor Bolts for Facility Area 5 & 10 (172Nos)	9	25-Apr-17	05-May-17																
0330-1071	Installation of Post (43Nos)	9	28-Apr-17	09-May-17																
0330-1073	Construction of Steel Roof	9	04-May-17	13-May-17																
0330-1075	Sprinkler System Installation	10	09-May-17	19-May-17																
0330-1077	T & C of Sprinkler System	6	20-May-17	26-May-17																
0330-1079	Drilling for Post Anchor Bolts for Facility Area 6, 8 & 9 (292Nos)	15	08-May-17	24-May-17																
0330-1081	Installation of Post (73Nos)	15	12-May-17	29-May-17																
0330-1083	Breaking Slab & Connection to Existing Draw Pits	14	11-May-17	26-May-17																
0330-1085	Breaking Slab & Excavate for Draw Pits (17Nos)	15	27-May-17	14-Jun-17																
0330-1087	Construction of Draw Pits (3 Gang @ 6d/Pit)	36	02-Jun-17	14-Jul-17																
0330-1089	BackFilling Works around Draw Pits	7	15-Jul-17	22-Jul-17																
0330-1093	Construction of U-Channels	33	02-Jun-17	11-Jul-17																
05 - SECTION 2 & 2A OF THE WORKS																				
05.1 - Cut & Cover Tunnel Ch 4855-4932 (APS Footprint)																				
05.1.6 - EVB Sub-structure & Tunnel																				
05.1.7 - EVB & Tunnel Remedial Works																				
A2273	EVB - Rectification of Concrete Defects at Stairs 01 & 6	6	20-Dec-16 A	26-Apr-17																
A4870	APS - B2M Southern Wall	6	11-Mar-17 A	26-Apr-17																
09 - SECTION 6 OF THE WORKS																				
09.1 - Carparks for Harbour Grand Hong Kong																				
HGHK Reprovision																				
Design, Submission, Material Approval																				
Testing and Commissioning																				

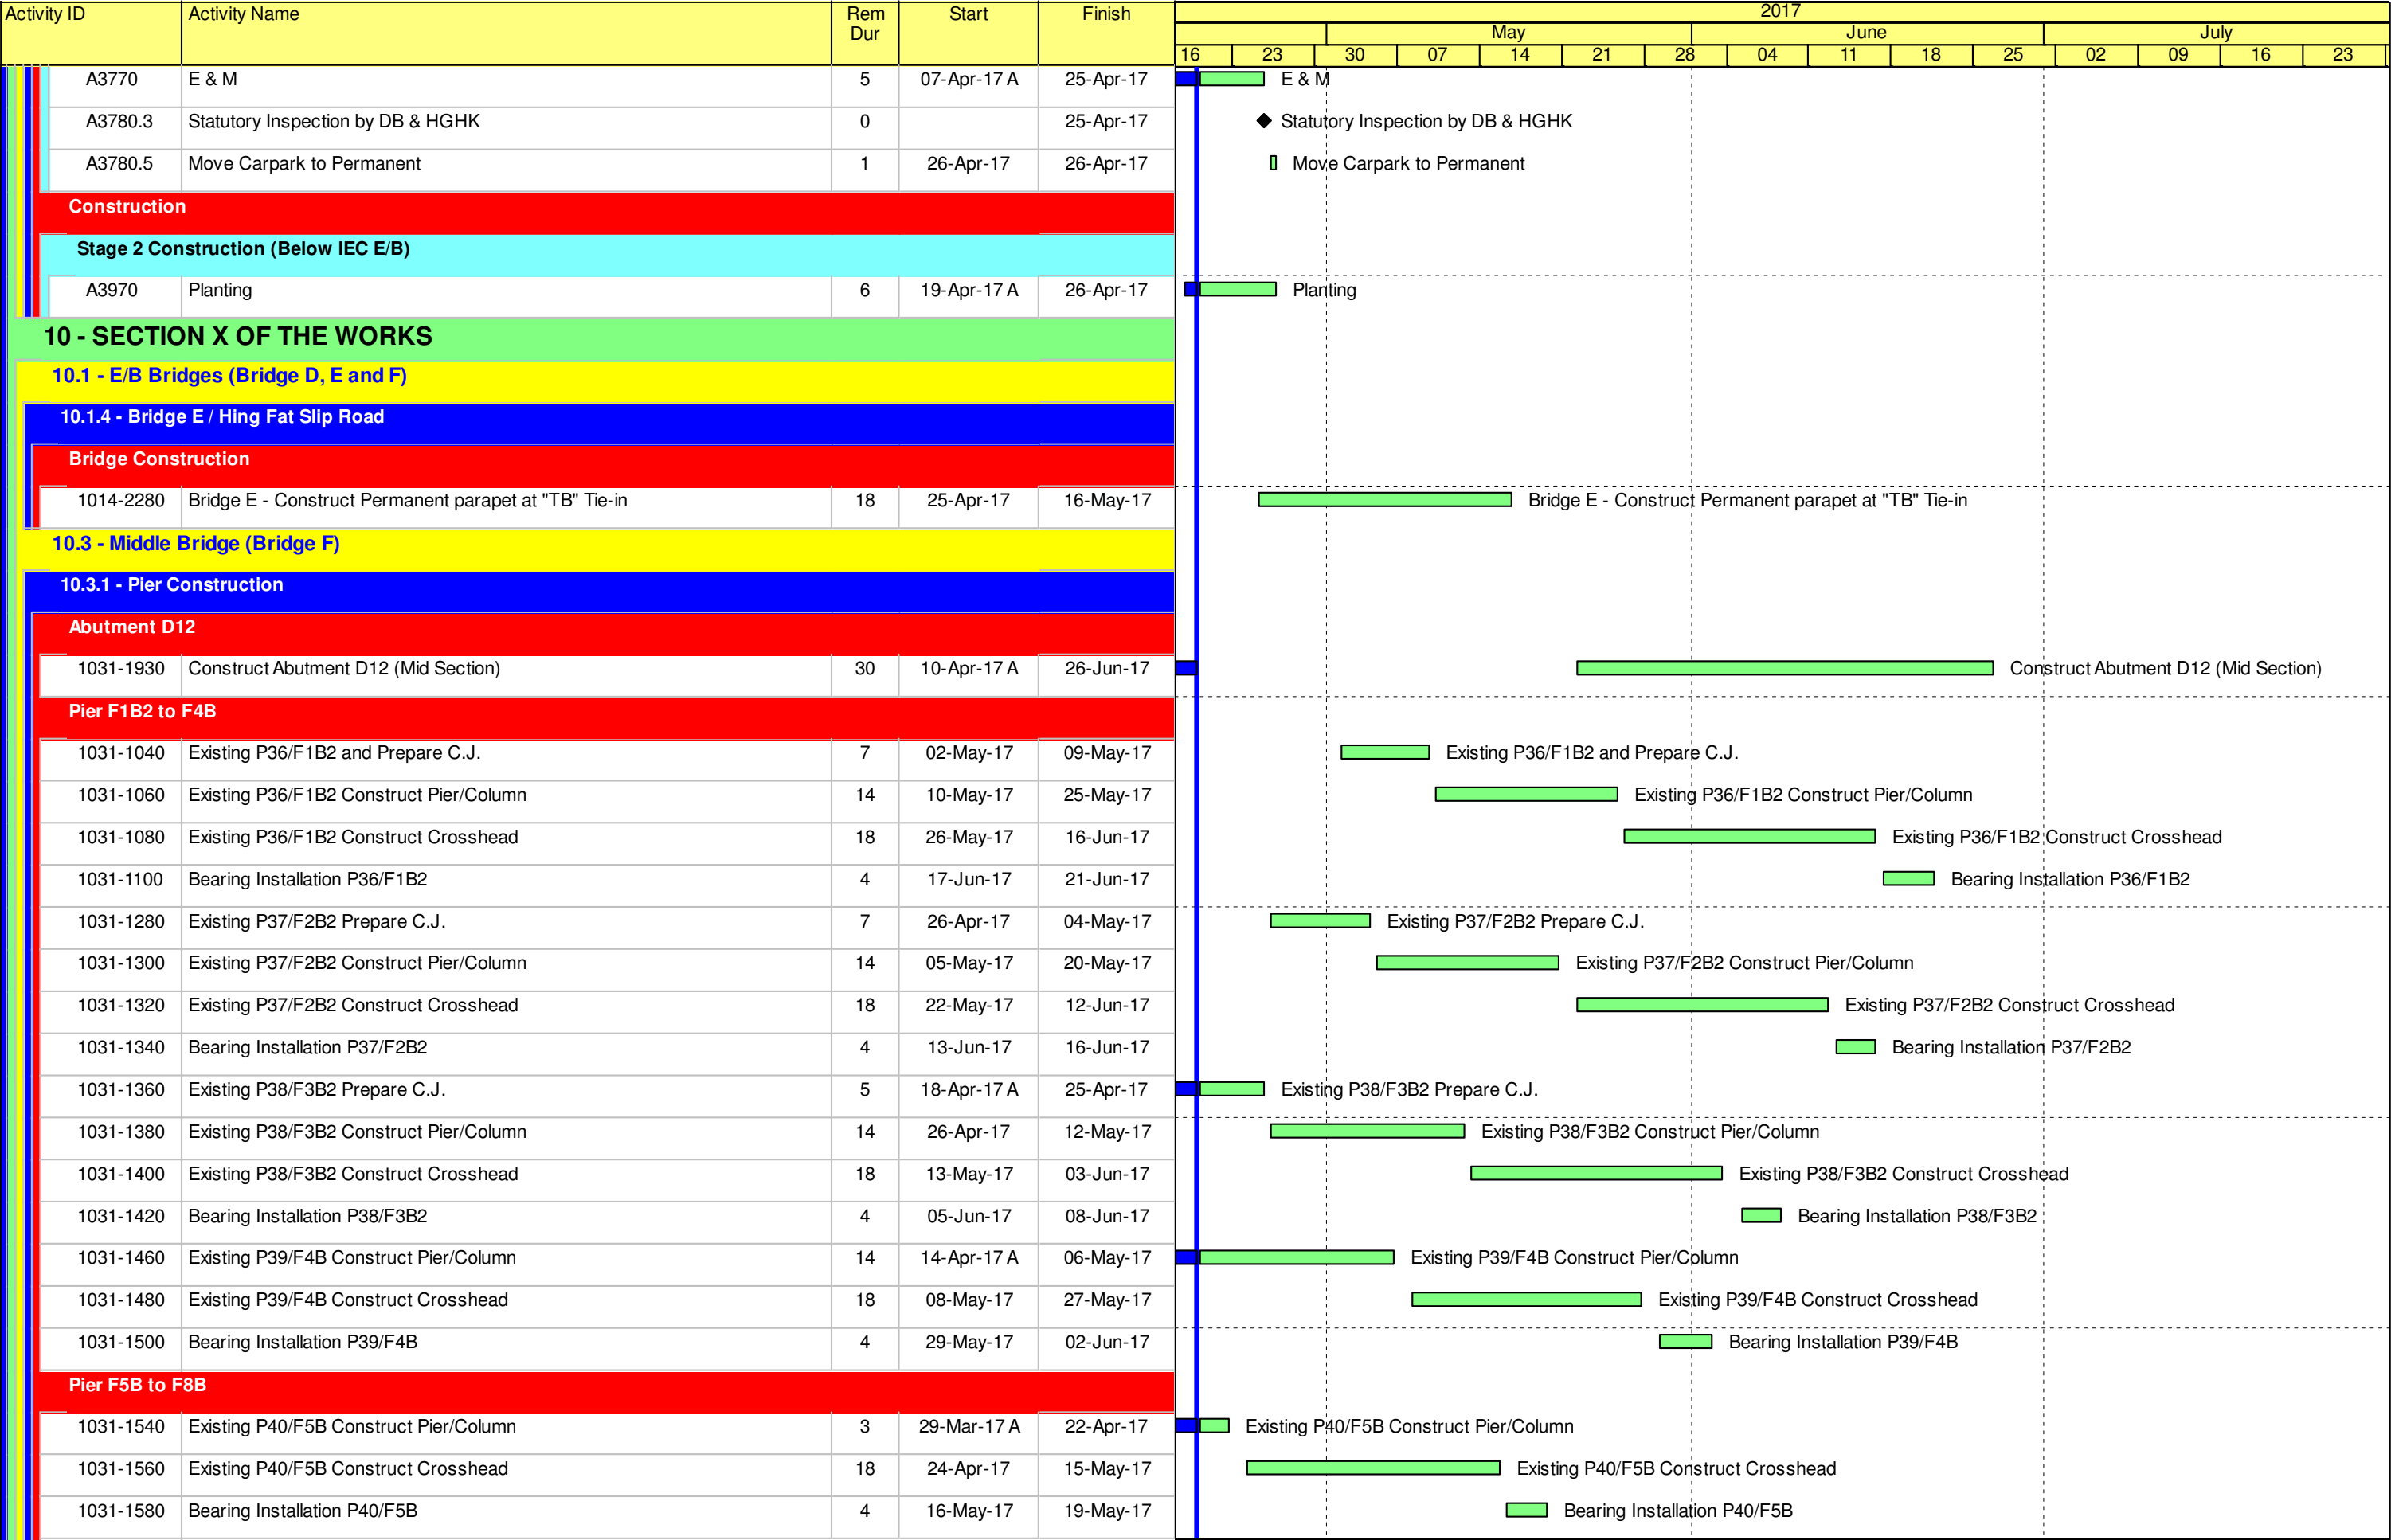

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
					May						June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
1031-1640	Existing P41/F6B Construct Crosshead	13	10-Apr-17 A	05-May-17	Existing P41/F6B Construct Crosshead															
1031-1660	Bearing Installation P41/F6B	4	06-May-17	10-May-17	Bearing Installation P41/F6B															
1031-1720	Existing P42/F7B Construct Crosshead	8	24-Mar-17 A	28-Apr-17	Existing P42/F7B Construct Crosshead															
1031-1740	Bearing Installation P42/F7B	4	29-Apr-17	04-May-17	Bearing Installation P42/F7B															
1031-1800	Existing P43/F8B Construct Crosshead	3	17-Mar-17 A	22-Apr-17	Existing P43/F8B Construct Crosshead															
1031-1820	Upstand Wall + Bearing Installation P43/F8B	11	24-Apr-17	06-May-17	Upstand Wall + Bearing Installation P43/F8B															
10.3.2 - Bridge Construction																				
Bridge F3B																				
1032-1840	LG-A Launching - Engage FL at F7B/Pier42	2	08-May-17	09-May-17	LG-A Launching - Engage FL at F7B/Pier42															
1032-1860	P42/F7B - Install Pier Segment - Place Pier Segment	1	10-May-17	10-May-17	P42/F7B - Install Pier Segment - Place Pier Segment															
1032-1880	P42/F7B - Install Pier Segment - Adjust Segment Level and Location	2	11-May-17	12-May-17	P42/F7B - Install Pier Segment - Adjust Segment Level and Location															
1032-1900	P42/F7B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	13-May-17	15-May-17	P42/F7B - Install Pier Segment - Grouting the Bearing Upper Plinth															
1032-1920	P42/F7B - Install Pier Segment - Stressing Nailing	2	16-May-17	17-May-17	P42/F7B - Install Pier Segment - Stressing Nailing															
1032-1940	LG-A Launching - Install MS at P42/F7B	1	18-May-17	18-May-17	LG-A Launching - Install MS at P42/F7B															
1032-1960	LG-A Launching - Deactivate the MS at F9B/Pier44 and Engage FL at P41/F6B	2	19-May-17	20-May-17	LG-A Launching - Deactivate the MS at F9B/Pier44 and Engage FL at P41/F6B															
1032-1980	P41/F6B - Install Pier Segment - Place Pier Segment	1	22-May-17	22-May-17	P41/F6B - Install Pier Segment - Place Pier Segment															
1032-2000	P41/F6B - Install Pier Segment - Adjust Segment Level and Location	2	23-May-17	24-May-17	P41/F6B - Install Pier Segment - Adjust Segment Level and Location															
1032-2020	P41/F6B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	25-May-17	26-May-17	P41/F6B - Install Pier Segment - Grouting the Bearing Upper Plinth															
1032-2040	P41/F6B - Install Pier Segment - Stressing Nailing	2	27-May-17	29-May-17	P41/F6B - Install Pier Segment - Stressing Nailing															
1032-2060	P41/F6B - Install Pier Segment - Install MS at F6B/Pier41	1	31-May-17	31-May-17	P41/F6B - Install Pier Segment - Install MS at F6B/Pier41															
1032-2080	P42/F7B - T Span Erection (5 pairs)	4	01-Jun-17	05-Jun-17	P42/F7B - T Span Erection (5 pairs)															
1032-2100	P43/F8B(MJ Left) - End Span Erection - Hanging Segments	3	06-Jun-17	08-Jun-17	P43/F8B(MJ Left) - End Span Erection - Hanging Segments															
1032-2120	P43/F8B(MJ Left) - End Span Erection - Erect Segments	1	09-Jun-17	09-Jun-17	P43/F8B(MJ Left) - End Span Erection - Erect Segments															
1032-2140	P43/F8B(MJ Left) - End Span Erection - Stitching	2	10-Jun-17	12-Jun-17	P43/F8B(MJ Left) - End Span Erection - Stitching															
1032-2160	P43/F8B(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing	2	10-Jun-17	12-Jun-17	P43/F8B(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing															
1032-2180	P43/F8B(MJ Left) - End Span Erection - Prestress Span Tendons	2	13-Jun-17	14-Jun-17	P43/F8B(MJ Left) - End Span Erection - Prestress Span Tendons															
1032-2200	P43/F8B(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	15-Jun-17	15-Jun-17	P43/F8B(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork															
1032-2220	LG-A Launching - Deactivate the MS at F8B/Pier43 and Engage FL at P40/F5B	2	16-Jun-17	17-Jun-17	LG-A Launching - Deactivate the MS at F8B/Pier43 and Engage FL at P40/F5B															
1032-2240	P41/F6B - T Span Erection (6 pairs)	4	19-Jun-17	22-Jun-17	P41/F6B - T Span Erection (6 pairs)															
1032-2260	P40/F5B - Install Pier Segment - Place Pier Segment (2nos.)	2	19-Jun-17	20-Jun-17	P40/F5B - Install Pier Segment - Place Pier Segment (2nos.)															
1032-2280	P40/F5B - Install Pier Segment - Adjust Segment Level and Location	3	21-Jun-17	23-Jun-17	P40/F5B - Install Pier Segment - Adjust Segment Level and Location															
1032-2300	P40/F5B - Install Pier Segment - Install the Tie & Packing System	2	24-Jun-17	26-Jun-17	P40/F5B - Install Pier Segment - Install the Tie & Packing System															
1032-2320	P40/F5B - Install Pier Segment - Install MS at P40/F5B (Right) and Engage FL at P39/F4B	2	27-Jun-17	28-Jun-17	P40/F5B - Install Pier Segment - Install MS at P40/F5B (Right) and Engage FL at P39/F4B															
1032-2340	P40/F5B(MJ Right) - End Span Erection - Hanging Segments	2	29-Jun-17	30-Jun-17	P40/F5B(MJ Right) - End Span Erection - Hanging Segments															
1032-2360	P40/F5B(MJ Right) - End Span Erection - Erect Segments	1	03-Jul-17	03-Jul-17	P40/F5B(MJ Right) - End Span Erection - Erect Segments															

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 4 of 9

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																	
									May				June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23			
	1032-2380	P40/F5B(MJ Right) - End Span Erection - Stitching	2	04-Jul-17	05-Jul-17														P40/F5B(MJ Right) - End Span Erection -			
	1032-2400	P40/F5B(MJ Right) - End Span Erection - Formwork Fixing for and Grouting for Bearing	2	04-Jul-17	05-Jul-17														P40/F5B(MJ Right) - End Span Erection -			
	1032-2420	P40/F5B(MJ Right) - End Span Erection - Prestress Span Tendons	2	06-Jul-17	07-Jul-17														P40/F5B(MJ Right) - End Span Erection -			
	1032-2440	P40/F5B(MJ Right) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	08-Jul-17	08-Jul-17														P40/F5B(MJ Right) - End Span Erection -			
	1032-2460	Prestress Extenral Tendon Bridge F3B	10	10-Jul-17	20-Jul-17														Prestress Erection -			
Bridge F2B																						
	1032-2580	P39/F4B - Install Pier Segment - Place Pier Segment	1	04-Jul-17	04-Jul-17														P39/F4B - Install Pier Segment - Place			
	1032-2600	P39/F4B - Install Pier Segment - Adjust Segment Level and Location	2	05-Jul-17	06-Jul-17														P39/F4B - Install Pier Segment - Adjust			
	1032-2620	P39/F4B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	07-Jul-17	08-Jul-17														P39/F4B - Install Pier Segment - Grouting			
	1032-2640	P39/F4B - Install Pier Segment - Stressing Nailing	2	10-Jul-17	11-Jul-17														P39/F4B - Install Pier Segment - Stressing			
	1032-2660	P39/F4B - Install MS at P39/F4B	2	12-Jul-17	13-Jul-17														P39/F4B - Install MS at P39/F4B			
	1032-2680	P39/F4B - Install Pier Segment - Relocate MS at P40/F5B to left and Engage FL at P39/F3B	2	14-Jul-17	15-Jul-17														P39/F4B - Install Pier Segment - Relocate			
	1032-2700	P39/F4B - T Span Erection (6 pairs)	4	17-Jul-17	20-Jul-17														P39/F4B - T Span Erection (6 pairs)			
All Middle Bridge F (Common)																						
	1032-4350	TCSS/LV Ducts at Pier 50-51	14	27-Apr-17	13-May-17			TCSS/LV Ducts at Pier 50-51														
	1032-4353	TCSS/LV Ducts at Pier 51-52	14	15-May-17	31-May-17				TCSS/LV Ducts at Pier 51-52													
	1032-4354	TCSS/LV Ducts at Pier 52-53	14	01-Jun-17	16-Jun-17					TCSS/LV Ducts at Pier 52-53												
	1032-4355	TCSS/LV Ducts at Pier 53-54	14	17-Jun-17	04-Jul-17						TCSS/LV Ducts at Pier 53-54											
	1032-4356	TCSS/LV Ducts at Pier 55-56	14	05-Jul-17	20-Jul-17							TCSS/LV Ducts at Pier 55-56										
10.4 - Bridge Deck Demolition																						
10.4.3 - Existing E/B Bridge																						
	10412-1650	Demolish Dolphin + Tie Beam & Reconstruct Tie Beam Pier 34	20	19-Jun-17	12-Jul-17										Demolish Dolphin + Tie Beam & Reconstruct Tie Beam Pier 34							
	10412-1670	Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 34 & 35 by Crane	9	08-Jun-17	17-Jun-17									Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 34 & 35 by Crane								
	10412-1700	Demolish Dolphin+Pile Cap & Reconstruct Pier 33 Pile Cap	20	19-Jun-17	12-Jul-17										Demolish Dolphin+Pile Cap & Reconstruct Pier 33 Pile Cap							
	10412-1710	Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 33	9	27-May-17	07-Jun-17					Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 33												
	10412-1720	Demolish Temp. E/B Bridge - Deck > Pier 33 to 34 (6 beams)	5	22-May-17	26-May-17				Demolish Temp. E/B Bridge - Deck > Pier 33 to 34 (6 beams)													
	10412-1730	Demolish Dolphin+Pile Cap & Reconstruct Pier 32 Pile Cap	20	08-Jun-17	30-Jun-17									Demolish Dolphin+Pile Cap & Reconstruct Pier 32 Pile Cap								
	10412-1760	Demolish Dolphin+Pile Cap & Reconstruct Pier 31 Pile Cap	20	08-Mar-17 A	13-May-17		Demolish Dolphin+Pile Cap & Reconstruct Pier 31 Pile Cap															
	10412-1790	Demolish Dolphin+Pile Cap & Reconstruct Pier 30 Pile Cap	20	02-Mar-17 A	13-May-17		Demolish Dolphin+Pile Cap & Reconstruct Pier 30 Pile Cap															
	A3430	Demolish Pier + Steel Support at Pier 36	9	20-Apr-17 A	29-Apr-17		Demolish Pier + Steel Support at Pier 36															
	A3440	Launch LG-BM to next Bridge Span	1	02-May-17	02-May-17			Launch LG-BM to next Bridge Span														
	A3450	Demolish Four(4nos) Beams at Pier 35-34 - by LG-BM	2	03-May-17	04-May-17			Demolish Four(4nos) Beams at Pier 35-34 - by LG-BM														
	A3460	Dismantle LGB	14	05-May-17	20-May-17			Dismantle LGB														
10.5 - Temporary Bridge																						
10.5.2 - Temporary Bridge 'TB'																						

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
					May						June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
1052-1260	TB > Demolition of Temporary Bridge "TB"	4	03-Apr-17 A	24-Apr-17	TB > Demolition of Temporary Bridge "TB"															
10.6 - Tunnel Approach Ramp																				
10.6.1 - Approach Ramp (Excluding Portion IIB)																				
Piling Works																				
1061-3490	Moving Temp Car Park to Permanent Car Park Completed	0		27-Apr-17	◆ Moving Temp Car Park to Permanent Car Park Completed															
1061-3500	Pre Bored H-Pile > Pile Ramp - BM03 A	4	27-Apr-17	02-May-17	■ Pre Bored H-Pile > Pile Ramp - BM03 A															
1061-3520	Pre Bored H-Pile > Pile Ramp - BM03 A - (H-Pile + Grouting)	1	03-May-17	03-May-17	■ Pre Bored H-Pile > Pile Ramp - BM03 A - (H-Pile + Grouting)															
1061-3540	Pre Bored H-Pile > Pile Ramp - BM03 B	4	03-May-17	06-May-17	■ Pre Bored H-Pile > Pile Ramp - BM03 B															
1061-3560	Pre Bored H-Pile > Pile Ramp - BM03 B - (H-Pile + Grouting)	1	08-May-17	08-May-17	■ Pre Bored H-Pile > Pile Ramp - BM03 B - (H-Pile + Grouting)															
1061-3820	Pre Bored H-Pile > Pile Ramp - BN11 A(Low Head Rm)	8	08-May-17	16-May-17	■ Pre Bored H-Pile > Pile Ramp - BN11 A(Low Head Rm)															
1061-3840	Pre Bored H-Pile > Pile Ramp - BN11 A - (H-Pile + Grouting)	1	17-May-17	17-May-17	■ Pre Bored H-Pile > Pile Ramp - BN11 A - (H-Pile + Grouting)															
1061-3860	Pre Bored H-Pile > Pile Ramp - BN11 B (LHR)	8	08-May-17	16-May-17	■ Pre Bored H-Pile > Pile Ramp - BN11 B (LHR)															
1061-3880	Pre Bored H-Pile > Pile Ramp - BN11 B - (H-Pile + Grouting)	1	17-May-17	17-May-17	■ Pre Bored H-Pile > Pile Ramp - BN11 B - (H-Pile + Grouting)															
1061-3900	Pre Bored H-Pile > Pile Ramp - BN12 A (LHR)	8	17-May-17	25-May-17	■ Pre Bored H-Pile > Pile Ramp - BN12 A (LHR)															
1061-3920	Pre Bored H-Pile > Pile Ramp - BN12 A - (H-Pile + Grouting)	1	26-May-17	26-May-17	■ Pre Bored H-Pile > Pile Ramp - BN12 A - (H-Pile + Grouting)															
1061-3940	Pre Bored H-Pile > Pile Ramp - BN12 B (LHR)	8	17-May-17	25-May-17	■ Pre Bored H-Pile > Pile Ramp - BN12 B (LHR)															
1061-3960	Pre Bored H-Pile > Pile Ramp - BN12 B - (H-Pile + Grouting)	1	26-May-17	26-May-17	■ Pre Bored H-Pile > Pile Ramp - BN12 B - (H-Pile + Grouting)															
1061-3980	Pre Bored H-Pile > Pile Ramp - BN13 A (LHR)	8	26-May-17	05-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN13 A (LHR)															
1061-4000	Pre Bored H-Pile > Pile Ramp - BN13 A - (H-Pile + Grouting)	1	06-Jun-17	06-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN13 A - (H-Pile + Grouting)															
1061-4020	Pre Bored H-Pile > Pile Ramp - BN13 B (LHR)	8	26-May-17	05-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN13 B (LHR)															
1061-4040	Pre Bored H-Pile > Pile Ramp - BN13 B - (H-Pile + Grouting)	1	06-Jun-17	06-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN13 B - (H-Pile + Grouting)															
1061-4060	Pre Bored H-Pile > Pile Ramp - BN01 A (LHR)	8	06-Jun-17	14-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN01 A (LHR)															
1061-4080	Pre Bored H-Pile > Pile Ramp - BN01 A - (H-Pile + Grouting)	1	15-Jun-17	15-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN01 A - (H-Pile + Grouting)															
1061-4100	Pre Bored H-Pile > Pile Ramp - BN01 B (LHR)	8	06-Jun-17	14-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN01 B (LHR)															
1061-4120	Pre Bored H-Pile > Pile Ramp - BN01 B - (H-Pile + Grouting)	1	15-Jun-17	15-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN01 B - (H-Pile + Grouting)															
1061-4140	Pre Bored H-Pile > Pile Ramp - BN05 A (LHR)	8	15-Jun-17	23-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN05 A (LHR)															
1061-4160	Pre Bored H-Pile > Pile Ramp - BN05 A - (H-Pile + Grouting)	1	24-Jun-17	24-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN05 A - (H-Pile + Grouting)															
1061-4180	Pre Bored H-Pile > Pile Ramp - BN05 B (LHR)	8	15-Jun-17	23-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN05 B (LHR)															
1061-4200	Pre Bored H-Pile > Pile Ramp - BN05 B - (H-Pile + Grouting)	1	24-Jun-17	24-Jun-17	■ Pre Bored H-Pile > Pile Ramp - BN05 B - (H-Pile + Grouting)															
1061-4220	Pre Bored H-Pile > Pile Ramp - BN06 A (LHR)	8	24-Jun-17	04-Jul-17	■ Pre Bored H-Pile > Pile Ramp - BN06 A (LHR)															
1061-4240	Pre Bored H-Pile > Pile Ramp - BN06 A - (H-Pile + Grouting)	1	05-Jul-17	05-Jul-17	■ Pre Bored H-Pile > Pile Ramp - BN06 A - (H-Pile + Grouting)															
1061-4260	Pre Bored H-Pile > Pile Ramp - BN06 B (LHR)	8	24-Jun-17	04-Jul-17	■ Pre Bored H-Pile > Pile Ramp - BN06 B (LHR)															
1061-4280	Pre Bored H-Pile > Pile Ramp - BN06 B - (H-Pile + Grouting)	1	05-Jul-17	05-Jul-17	■ Pre Bored H-Pile > Pile Ramp - BN06 B - (H-Pile + Grouting)															
1061-4300	Remaining Bored Piles & Pre-Bored H-Pile Testing	30	31-May-17	05-Jul-17	■ Remaining Bored Piles & Pre-Bored H-Pile Testing															
Excavation & ELS Works																				

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 6 of 9

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																																								
							May				June				July																														
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23																										
1061-4901.2	Sheet Piling Works (WF1>B3:19m@1.5m/d) (incl Re-boring & Welding Remedial Works)	9	12-Jul-16 A	29-Apr-17			Sheet Piling Works (WF1>B3:19m@1.5m/d) (incl Re-boring & Welding Remedial Works)																																						
1061-4910	Advance Sheet Piling Works + Pre-drilling in Phase 2 - Cul de sac Area (30m)	14	04-Apr-17 A	17-May-17				Advance Sheet Piling Works + Pre-drilling in Phase 2 - Cul de sac Area (30m)																																					
1061-4915	Tam Grouting	12	14-Sep-16 A	04-May-17			Tam Grouting																																						
1061-5060	Dewatering Well Installation (14Nos)	9	11-Jan-17 A	29-Apr-17			Dewatering Well Installation (14Nos)																																						
1061-5080	Observation Well Installation (10Nos)	9	13-Feb-17 A	29-Apr-17			Observation Well Installation (10Nos)																																						
1061-5100	Pumping Test	9	05-May-17	15-May-17				Pumping Test																																					
1061-5120	Complete Pump Test	0		15-May-17				◆ Complete Pump Test																																					
1061-5140	Ch 5285 - 5331 > Excav from Ex. Lvl down to 2.5mPD (Ch 5285 - 5331 w/ open cut)	7	15-Aug-16 A	27-Apr-17			Ch 5285 - 5331 > Excav from Ex. Lvl down to 2.5mPD (Ch 5285 - 5331 w/ open cut)																																						
1061-5160	Ch 5234 - 5285 > Excav from Ex. Lvl down to 2.5mPD	9	30-Mar-17 A	09-May-17				Ch 5234 - 5285 > Excav from Ex. Lvl down to 2.5mPD																																					
1061-5180	Ch 5234 - 5285 > Install 1st Layer of Strut & Waling	9	10-May-17	19-May-17				Ch 5234 - 5285> Install 1st Layer of Strut & Waling																																					
1061-5200	Ch 5234 - 5285 > Excav from 2.5mPD to 1m Below 2nd Layer of Struts	16	20-May-17	08-Jun-17				Ch 5234 - 5285 > Excav from 2.5mPD to 1m Below 2nd Layer of Struts																																					
1061-5220	Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling	9	09-Jun-17	19-Jun-17					Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling																																				
1061-5240	Ch 5234 - 5285 > Excav to FEL	13	20-Jun-17	05-Jul-17						Ch 5234 - 5285 > Excav to FEL																																			
Structure Works																																													
1061-5260	Bay 1 - Ch 5322 - 5331 > Base Slab - Blinding Layer	1	09-Jun-17	09-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Blinding Layer																															
1061-5280	Bay 1 - Ch 5322 - 5331 > Base Slab - Water Proofing Membrane	2	10-Jun-17	12-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Water Proofing Membrane																															
1061-5300	Bay 1 - Ch 5322 - 5331 > Base Slab - Rebar Fixing	5	13-Jun-17	17-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Rebar Fixing																															
1061-5320	Bay 1 - Ch 5322 - 5331 > Base Slab - Erect Formworks	4	19-Jun-17	22-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Erect Formwo																															
1061-5340	Bay 1 - Ch 5322 - 5331 > Base Slab - Concreting	1	23-Jun-17	23-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Concreting																															
1061-5360	Bay 2 - Ch 5313 - 5322 > Base Slab - Blinding Layer	1	24-Jun-17	24-Jun-17										Bay 2 - Ch 5313 - 5322 > Base Slab - Blinding Lay																															
1061-5380	Bay 2 - Ch 5313 - 5322 > Base Slab - Water Proofing Membrane	2	26-Jun-17	27-Jun-17										Bay 2 - Ch 5313 - 5322 > Base Slab - Water P																															
1061-5400	Bay 2 - Ch 5313 - 5322 > Base Slab - Rebar Fixing	5	28-Jun-17	04-Jul-17										Bay 2 - Ch 5313 - 5322 > Base Slab																															
1061-5420	Bay 2 - Ch 5313 - 5322 > Base Slab - Erect Formworks	4	05-Jul-17	08-Jul-17										Bay 2 - Ch 5313 - 5322 > Bas																															
1061-5440	Bay 2 - Ch 5313 - 5322 > Base Slab - Concreting	1	10-Jul-17	10-Jul-17										Bay 2 - Ch 5313 - 5322 > B																															
1061-5460	Bay 3 - Ch 5303 - 5313 > Base Slab - Blinding Layer	1	11-Jul-17	11-Jul-17										Bay 3 - Ch 5303 - 5313 >																															
1061-5480	Bay 3 - Ch 5303 - 5313 > Base Slab - Water Proofing Membrane	2	12-Jul-17	13-Jul-17										Bay 3 - Ch 5303 - 531																															
1061-5500	Bay 3 - Ch 5303 - 5313 > Base Slab - Rebar Fixing	5	14-Jul-17	19-Jul-17										Bay 3 - Ch 53																															
1061-5560	Bay 6 - Ch 5262 - 5277 > Base Slab - Blinding Layer	1	06-Jul-17	06-Jul-17										Bay 6 - Ch 5262 - 5277 > Base S																															
1061-5580	Bay 6 - Ch 5262 - 5277 > Base Slab - Water Proofing Membrane	2	07-Jul-17	08-Jul-17										Bay 6 - Ch 5262 - 5277 > Bas																															
1061-5600	Bay 6 - Ch 5262 - 5277 > Base Slab - Rebar Fixing	6	10-Jul-17	15-Jul-17										Bay 6 - Ch 5262 - 5																															
Retaining Walls & Trough Structure B,C & D																																													
1061-6860	Construct Retaining Wal E Pile Cap (7 nos)	24	06-Mar-17 A	18-May-17			Construct Retaining Wal E Pile Cap (7 nos)																																						
1061-6880	Construct Retaining Wal E1 (Ch 5332 - 5371)	18	19-May-17	09-Jun-17					Construct Retaining Wal E1 (Ch 5332 - 5371)																																				
1061-6900	Construct Retaining Wal E3 (Ch 5371 - 5398)	18	10-Jun-17	30-Jun-17						Construct Retaining Wall E3 (Ch 5371 - 5																																			
1061-6920	Construct Retaining Wal E3 (Ch 5398 - 5419)	18	19-May-17	09-Jun-17					Construct Retaining Wal E3 (Ch 5398 - 5419)																																				
Remaining Level of Effort		Remaining Work		Contract HY/2009/19 Three Months Rolling Programme (20 April 2017 to 19 July 2017)																																									
Actual Level of Effort		Critical Remaining Work																																											
Actual Work		Milestone																																											
Page 7 of 9																																													

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
							May				June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
10.6.2 - Approach Ramp (Within Portion IIB)																				
Pre-Bored H-Piles																				
1062-1020	Predrilling for ramp within Portion IIB (14no - 3set)	18	28-Apr-17	19-May-17	Predrilling for ramp within Portion IIB (14no - 3set)															
1062-1040	Approach Ramp Portion IIB Piles Final Report / Founding Level	18	08-May-17	27-May-17	Approach Ramp Portion IIB Piles Final Report / Founding Level															
1062-1400	Pre Bored H-Pile > Pile Ramp - BS01 A	14	15-May-17	31-May-17	Pre Bored H-Pile > Pile Ramp - BS01 A															
1062-1420	Pre Bored H-Pile > Pile Ramp - BS01 B	14	20-May-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BS01 B															
1062-1440	Pre Bored H-Pile > Pile Ramp - BS02 A	14	26-May-17	12-Jun-17	Pre Bored H-Pile > Pile Ramp - BS02 A															
1062-1460	Pre Bored H-Pile > Pile Ramp - BS02 B	14	02-Jun-17	17-Jun-17	Pre Bored H-Pile > Pile Ramp - BS02 B															
1062-1480	Pre Bored H-Pile > Pile Ramp - BS03 A	14	08-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BS03 A															
1062-1500	Pre Bored H-Pile > Pile Ramp - BS03 B	14	14-Jun-17	29-Jun-17	Pre Bored H-Pile > Pile Ramp - BS03 B															
1062-1520	Pre Bored H-Pile > Pile Ramp - BS04 A	14	20-Jun-17	06-Jul-17	Pre Bored H-Pile > Pile Ramp - BS04 A															
1062-1540	Pre Bored H-Pile > Pile Ramp - BS04 B	14	26-Jun-17	12-Jul-17	Pre Bored H-Pile > Pile Ramp - BS04 B															
1062-1560	Pre Bored H-Pile > Pile Ramp - BS05 A	14	15-May-17	31-May-17	Pre Bored H-Pile > Pile Ramp - BS05 A															
1062-1580	Pre Bored H-Pile > Pile Ramp - BS05 B	14	20-May-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BS05 B															
1062-1600	Pre Bored H-Pile > Pile Ramp - BS06 A	14	26-May-17	12-Jun-17	Pre Bored H-Pile > Pile Ramp - BS06 A															
1062-1620	Pre Bored H-Pile > Pile Ramp - BS06 B	14	02-Jun-17	17-Jun-17	Pre Bored H-Pile > Pile Ramp - BS06 B															
1062-1640	Pre Bored H-Pile > Pile Ramp - BS07 A	14	08-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BS07 A															
1062-1660	Pre Bored H-Pile > Pile Ramp - BS07 B	14	14-Jun-17	29-Jun-17	Pre Bored H-Pile > Pile Ramp - BS07 B															
1062-1680	Pre Bored H-Pile > Pile Ramp - BS08 A	14	20-Jun-17	06-Jul-17	Pre Bored H-Pile > Pile Ramp - BS08 A															
1062-1700	Pre Bored H-Pile > Pile Ramp - BS08 B	14	26-Jun-17	12-Jul-17	Pre Bored H-Pile > Pile Ramp - BS08 B															
1062-1720	Pre Bored H-Pile > Pile Ramp - BS09 A	14	20-May-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BS09 A															
1062-1740	Pre Bored H-Pile > Pile Ramp - BS09 B	14	26-May-17	12-Jun-17	Pre Bored H-Pile > Pile Ramp - BS09 B															
1062-1760	Pre Bored H-Pile > Pile Ramp - BS10 A	14	02-Jun-17	17-Jun-17	Pre Bored H-Pile > Pile Ramp - BS10 A															
1062-1780	Pre Bored H-Pile > Pile Ramp - BS10 B	14	08-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BS10 B															
1062-1800	Pre Bored H-Pile > Pile Ramp - BS11 A	14	14-Jun-17	29-Jun-17	Pre Bored H-Pile > Pile Ramp - BS11 A															
1062-1820	Pre Bored H-Pile > Pile Ramp - BS11 B	14	20-Jun-17	06-Jul-17	Pre Bored H-Pile > Pile Ramp - BS11 B															
1062-1840	Pre Bored H-Pile > Pile Ramp - BS12 A	14	26-Jun-17	12-Jul-17	Pre Bored H-Pile > Pile Ramp - BS12 A															
1062-1860	Pre Bored H-Pile > Pile Ramp - BS12 B	14	20-May-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BS12 B															
1062-1880	Pre Bored H-Pile > Pile Ramp - BS13 A	14	26-May-17	12-Jun-17	Pre Bored H-Pile > Pile Ramp - BS13 A															
1062-1900	Pre Bored H-Pile > Pile Ramp - BS13 B	14	02-Jun-17	17-Jun-17	Pre Bored H-Pile > Pile Ramp - BS13 B															
1062-1920	Pre Bored H-Pile >Pile Ramp - BM01 A	14	08-Jun-17	23-Jun-17	Pre Bored H-Pile >Pile Ramp - BM01 A															
1062-1940	Pre Bored H-Pile > Pile Ramp - BM01 B	14	14-Jun-17	29-Jun-17	Pre Bored H-Pile > Pile Ramp - BM01 B															
1062-1960	Pre Bored H-Pile > Pile Ramp - BM02 A	14	20-Jun-17	06-Jul-17	Pre Bored H-Pile > Pile Ramp - BM02 A															
1062-1980	Pre Bored H-Pile > Pile Ramp - BM02 B	14	26-Jun-17	12-Jul-17	Pre Bored H-Pile > Pile Ramp - BM02 B															
ELS																				

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

◆

 Milestone

◆

 Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 8 of 9

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																
									May				June				July				
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23		
	A1000	Sheet Pile and Preboring Works	61	09-May-17	20-Jul-17	Sheet Pile and Preboring Works															
	A1010	Dewatering System and Instrumentation installation	38	31-May-17	14-Jul-17	Dewatering System and Instrumentation installation															
10.7 - Section X - Miscellaneous Works																					
10.7.2 - Oil Street/Watson Road (Portion III)																					
	1072-1000	Remaining Fresh Water Main 200DI - F02 Portion VIIB (Watson/VB)	120	27-Apr-17	16-Sep-17	Remaining Fresh Water Main 200DI - F02 Portion VIIB (Watson/VB)															
	1072-1020	Remaining Storm Water Drain Portion VII (Watson/VB)	120	27-Apr-17	16-Sep-17	Remaining Storm Water Drain Portion VII (Watson/VB)															
	1072-1040	Fresh Water Main 100DI - F03 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Fresh Water Main 100DI - F03 Portion III (Oil Street/Admin Bldg)															
	1072-1060	Salt Water Main 100DI - S03 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Salt Water Main 100DI - S03 Portion III (Oil Street/Admin Bldg)															
	1072-1065	Salt Water Main 100DI - S02 (Watson rd - Previously at Portion XIIB)	50	27-Apr-17	26-Jun-17	Salt Water Main 100DI - S02 (Watson rd - Previously at Portion XIIB)															
	1072-1080	Foul Sewer Dia. 225 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Foul Sewer Dia. 225 Portion III (Oil Street/Admin Bldg)															
10.7.3 - Open Area																					
	1073-1010	Open Area - Pedestrian Parapet -Ch570.40 to Ch540.00	14	22-May-17*	07-Jun-17	Open Area - Pedestrian Parapet -Ch570.40 to Ch540.00															
	1073-1010.3	Open Area - Pedestrian Parapet - Ch540.00 to Ch520.00	14	08-Jun-17	23-Jun-17	Open Area - Pedestrian Parapet - Ch540.00 to Ch520.00															
	1073-1010.5	Open Area - Pedestrian Parapet - Ch0.00 - Ch40.00	14	24-Jun-17	11-Jul-17	Open Area - Pedestrian Parapet - Ch0.00 - Ch40.00															
	1073-1010.7	Open Area - Pedestrian Parapet - Ch40.00 - 80.00	14	12-Jul-17	27-Jul-17	Open Area - Pedestrian Parapet - Ch40.00 - 80.00															
11 - SECTION 11 OF THE WORKS																					
11.1 - Portion XIIA - Stage 1																					
11.1.1 - Along Watson Road - Waterwork & Roadworks (Portion XIIA)																					
	1110-2820	Permanent Cul-de Sac - Constr. of drainage	25	20-Apr-17*	19-May-17	Permanent Cul-de Sac - Constr. of drainage															
	1110-2830	Permanent Cul-de Sac - Constr. of watermains	25	03-May-17	01-Jun-17	Permanent Cul-de Sac - Constr. of watermains															
	1110-2840	Permanent Cul-de Sac - Constr. of public lighting & telecom (conduits & drawpits)	25	15-May-17	13-Jun-17	Permanent Cul-de Sac - Constr. of public lighting & telecom (conduits & drawpits)															
	1110-2850	Permanent Cul-de Sac - Constr. of (kerbs & pavements)	25	14-Jun-17	13-Jul-17	Permanent Cul-de Sac - Constr. of (kerbs & pavements)															
11.1.3 - Along Tsing Fung St. - TCSS cable ducting (Portion XIIA)																					
	1110-2930	TCSS cable ducting along Tsing Fung St	36	08-May-17*	19-Jun-17	TCSS cable ducting along Tsing Fung St															
11.1.4 - Along Gordon House - Cross road ducting at Hing Fat St adjacent to (Portion XIIA)																					
	1110-2940	Trench 1 (E&M, PL) - (Night Work)	16	19-Sep-16 A	09-May-17	Trench 1 (E&M, PL) - (Night Work)															
	1110-2950	Trench 2 (ATC) - (Night Work)	38	10-May-17	23-Jun-17	Trench 2 (ATC) - (Night Work)															
11.1.5 - Footing and frame/pole for directional sign FVMSH2, ADS16 and OHVD (Portion XIIA)																					
	1110-2960	ADS16	26	14-Sep-16 A	20-May-17	ADS16															
	1110-2970	OHVD	12	22-May-17	05-Jun-17	OHVD															
	1110-2980	FVMSH2	18	06-Jun-17	26-Jun-17	FVMSH2															

Remaining Level of Effort

Actual Level of Effort


Actual Work

Remaining Work

Critical Remaining Work

Milestone

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
									May				June				July			
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
0330-1043	Construction of Brace Footing	5	10-May-17	15-May-17																
0330-1047	Erection of Bracing Beam (3Nos)	3	16-May-17	18-May-17																
0330-1049	Touch-up Painting	12	22-May-17	05-Jun-17																
0330-1051	Waterproofing & Slab Reinstatement	7	19-May-17	26-May-17																
0330-1053	Breaking Slab & Excavate for Lamp Pole Footing	7	11-May-17	18-May-17																
0330-1055	Construction of Lamp Pole Footing (12Nos)	21	12-May-17	06-Jun-17																
0330-1057	Drilling for Lamp Pole at Existing Slab (8Nos Poles; M16-64Nos)	8	18-May-17	26-May-17																
0330-1059	Installation of Lamp Pole (total 20Nos)	14	23-May-17	08-Jun-17																
0330-1061	Breaking Existing Slab for Cross Road Ducting (Approx 300m)	18	24-May-17	14-Jun-17																
0330-1063	Laying Duct	5	15-Jun-17	20-Jun-17																
0330-1065	Cabling Works	9	21-Jun-17	30-Jun-17																
0330-1067	Slab Reinstatement	8	03-Jul-17	11-Jul-17																
0330-1069	Drilling for Post Anchor Bolts for Facility Area 5 & 10 (172Nos)	9	25-Apr-17	05-May-17																
0330-1071	Installation of Post (43Nos)	9	28-Apr-17	09-May-17																
0330-1073	Construction of Steel Roof	9	04-May-17	13-May-17																
0330-1075	Sprinkler System Installation	10	09-May-17	19-May-17																
0330-1077	T & C of Sprinkler System	6	20-May-17	26-May-17																
0330-1079	Drilling for Post Anchor Bolts for Facility Area 6, 8 & 9 (292Nos)	15	08-May-17	24-May-17																
0330-1081	Installation of Post (73Nos)	15	12-May-17	29-May-17																
0330-1083	Breaking Slab & Connection to Existing Draw Pits	14	11-May-17	26-May-17																
0330-1085	Breaking Slab & Excavate for Draw Pits (17Nos)	15	27-May-17	14-Jun-17																
0330-1087	Construction of Draw Pits (3 Gang @ 6d/Pit)	36	02-Jun-17	14-Jul-17																
0330-1089	BackFilling Works around Draw Pits	7	15-Jul-17	22-Jul-17																
0330-1093	Construction of U-Channels	33	02-Jun-17	11-Jul-17																
05 - SECTION 2 & 2A OF THE WORKS																				
05.1 - Cut & Cover Tunnel Ch 4855-4932 (APS Footprint)																				
05.1.6 - EVB Sub-structure & Tunnel																				
05.1.7 - EVB & Tunnel Remedial Works																				
A2273	EVB - Rectification of Concrete Defects at Stairs 01 & 6	6	20-Dec-16 A	26-Apr-17																
A4870	APS - B2M Southern Wall	6	11-Mar-17 A	26-Apr-17																
09 - SECTION 6 OF THE WORKS																				
09.1 - Carparks for Harbour Grand Hong Kong																				
HGHK Reprovision																				
Design, Submission, Material Approval																				
Testing and Commissioning																				

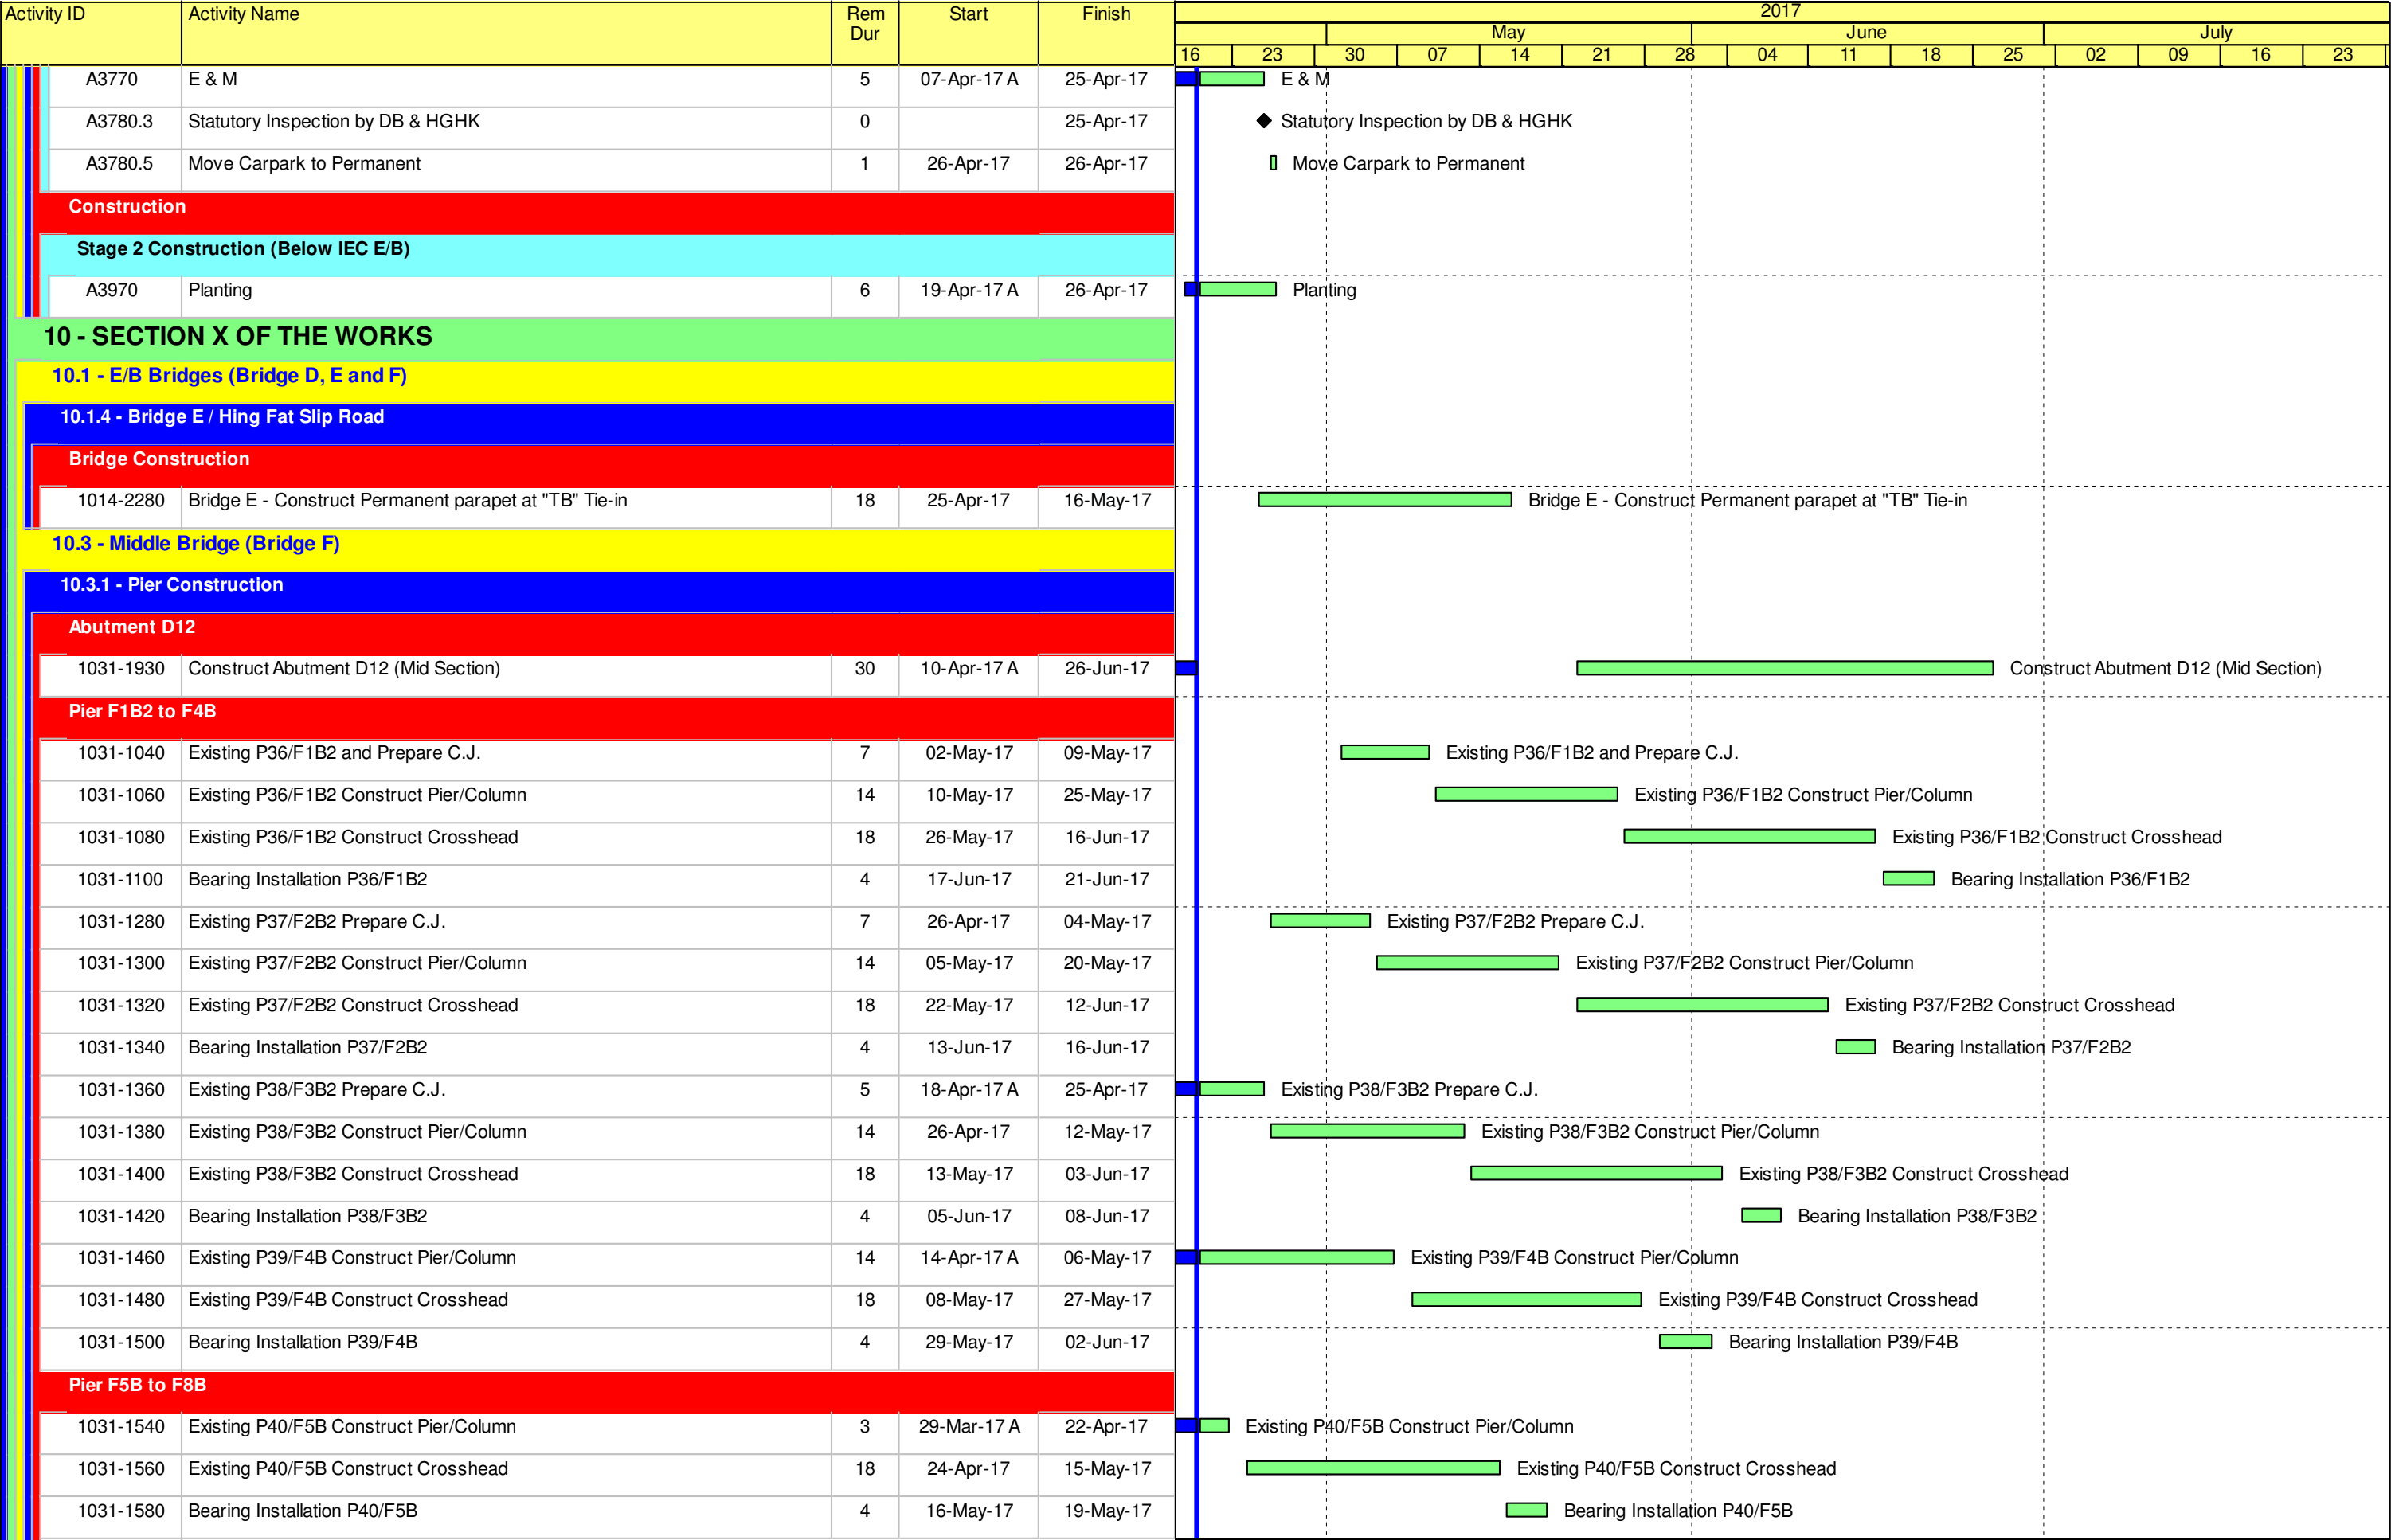

Activity ID	Activity Name	Rem Dur	Start	Finish	2017															
					May						June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
1031-1640	Existing P41/F6B Construct Crosshead	13	10-Apr-17 A	05-May-17	Existing P41/F6B Construct Crosshead															
1031-1660	Bearing Installation P41/F6B	4	06-May-17	10-May-17	Bearing Installation P41/F6B															
1031-1720	Existing P42/F7B Construct Crosshead	8	24-Mar-17 A	28-Apr-17	Existing P42/F7B Construct Crosshead															
1031-1740	Bearing Installation P42/F7B	4	29-Apr-17	04-May-17	Bearing Installation P42/F7B															
1031-1800	Existing P43/F8B Construct Crosshead	3	17-Mar-17 A	22-Apr-17	Existing P43/F8B Construct Crosshead															
1031-1820	Upstand Wall + Bearing Installation P43/F8B	11	24-Apr-17	06-May-17	Upstand Wall + Bearing Installation P43/F8B															
10.3.2 - Bridge Construction																				
Bridge F3B																				
1032-1840	LG-A Launching - Engage FL at F7B/Pier42	2	08-May-17	09-May-17	LG-A Launching - Engage FL at F7B/Pier42															
1032-1860	P42/F7B - Install Pier Segment - Place Pier Segment	1	10-May-17	10-May-17	P42/F7B - Install Pier Segment - Place Pier Segment															
1032-1880	P42/F7B - Install Pier Segment - Adjust Segment Level and Location	2	11-May-17	12-May-17	P42/F7B - Install Pier Segment - Adjust Segment Level and Location															
1032-1900	P42/F7B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	13-May-17	15-May-17	P42/F7B - Install Pier Segment - Grouting the Bearing Upper Plinth															
1032-1920	P42/F7B - Install Pier Segment - Stressing Nailing	2	16-May-17	17-May-17	P42/F7B - Install Pier Segment - Stressing Nailing															
1032-1940	LG-A Launching - Install MS at P42/F7B	1	18-May-17	18-May-17	LG-A Launching - Install MS at P42/F7B															
1032-1960	LG-A Launching - Deactivate the MS at F9B/Pier44 and Engage FL at P41/F6B	2	19-May-17	20-May-17	LG-A Launching - Deactivate the MS at F9B/Pier44 and Engage FL at P41/F6B															
1032-1980	P41/F6B - Install Pier Segment - Place Pier Segment	1	22-May-17	22-May-17	P41/F6B - Install Pier Segment - Place Pier Segment															
1032-2000	P41/F6B - Install Pier Segment - Adjust Segment Level and Location	2	23-May-17	24-May-17	P41/F6B - Install Pier Segment - Adjust Segment Level and Location															
1032-2020	P41/F6B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	25-May-17	26-May-17	P41/F6B - Install Pier Segment - Grouting the Bearing Upper Plinth															
1032-2040	P41/F6B - Install Pier Segment - Stressing Nailing	2	27-May-17	29-May-17	P41/F6B - Install Pier Segment - Stressing Nailing															
1032-2060	P41/F6B - Install Pier Segment - Install MS at F6B/Pier41	1	31-May-17	31-May-17	P41/F6B - Install Pier Segment - Install MS at F6B/Pier41															
1032-2080	P42/F7B - T Span Erection (5 pairs)	4	01-Jun-17	05-Jun-17	P42/F7B - T Span Erection (5 pairs)															
1032-2100	P43/F8B(MJ Left) - End Span Erection - Hanging Segments	3	06-Jun-17	08-Jun-17	P43/F8B(MJ Left) - End Span Erection - Hanging Segments															
1032-2120	P43/F8B(MJ Left) - End Span Erection - Erect Segments	1	09-Jun-17	09-Jun-17	P43/F8B(MJ Left) - End Span Erection - Erect Segments															
1032-2140	P43/F8B(MJ Left) - End Span Erection - Stitching	2	10-Jun-17	12-Jun-17	P43/F8B(MJ Left) - End Span Erection - Stitching															
1032-2160	P43/F8B(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing	2	10-Jun-17	12-Jun-17	P43/F8B(MJ Left) - End Span Erection - Formwork Fixing for and Grouting for Bearing															
1032-2180	P43/F8B(MJ Left) - End Span Erection - Prestress Span Tendons	2	13-Jun-17	14-Jun-17	P43/F8B(MJ Left) - End Span Erection - Prestress Span Tendons															
1032-2200	P43/F8B(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	15-Jun-17	15-Jun-17	P43/F8B(MJ Left) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork															
1032-2220	LG-A Launching - Deactivate the MS at F8B/Pier43 and Engage FL at P40/F5B	2	16-Jun-17	17-Jun-17	LG-A Launching - Deactivate the MS at F8B/Pier43 and Engage FL at P40/F5B															
1032-2240	P41/F6B - T Span Erection (6 pairs)	4	19-Jun-17	22-Jun-17	P41/F6B - T Span Erection (6 pairs)															
1032-2260	P40/F5B - Install Pier Segment - Place Pier Segment (2nos.)	2	19-Jun-17	20-Jun-17	P40/F5B - Install Pier Segment - Place Pier Segment (2nos.)															
1032-2280	P40/F5B - Install Pier Segment - Adjust Segment Level and Location	3	21-Jun-17	23-Jun-17	P40/F5B - Install Pier Segment - Adjust Segment Level and Location															
1032-2300	P40/F5B - Install Pier Segment - Install the Tie & Packing System	2	24-Jun-17	26-Jun-17	P40/F5B - Install Pier Segment - Install the Tie & Packing System															
1032-2320	P40/F5B - Install Pier Segment - Install MS at P40/F5B (Right) and Engage FL at P39/F4B	2	27-Jun-17	28-Jun-17	P40/F5B - Install Pier Segment - Install MS at P40/F5B (Right) and Engage FL at P39/F4B															
1032-2340	P40/F5B(MJ Right) - End Span Erection - Hanging Segments	2	29-Jun-17	30-Jun-17	P40/F5B(MJ Right) - End Span Erection - Hanging Segments															
1032-2360	P40/F5B(MJ Right) - End Span Erection - Erect Segments	1	03-Jul-17	03-Jul-17	P40/F5B(MJ Right) - End Span Erection - Erect Segments															

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 4 of 9

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																	
									May				June				July					
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23			
	1032-2380	P40/F5B(MJ Right) - End Span Erection - Stitching	2	04-Jul-17	05-Jul-17														P40/F5B(MJ Right) - End Span Erection -			
	1032-2400	P40/F5B(MJ Right) - End Span Erection - Formwork Fixing for and Grouting for Bearing	2	04-Jul-17	05-Jul-17														P40/F5B(MJ Right) - End Span Erection -			
	1032-2420	P40/F5B(MJ Right) - End Span Erection - Prestress Span Tendons	2	06-Jul-17	07-Jul-17														P40/F5B(MJ Right) - End Span Erection -			
	1032-2440	P40/F5B(MJ Right) - End Span Erection - Remove Hanger Bar & Hanger Beam & Stitching Formwork	1	08-Jul-17	08-Jul-17														P40/F5B(MJ Right) - End Span Erection -			
	1032-2460	Prestress Extenral Tendon Bridge F3B	10	10-Jul-17	20-Jul-17														Prestress Erection -			
Bridge F2B																						
	1032-2580	P39/F4B - Install Pier Segment - Place Pier Segment	1	04-Jul-17	04-Jul-17														P39/F4B - Install Pier Segment - Place			
	1032-2600	P39/F4B - Install Pier Segment - Adjust Segment Level and Location	2	05-Jul-17	06-Jul-17														P39/F4B - Install Pier Segment - Adjust			
	1032-2620	P39/F4B - Install Pier Segment - Grouting the Bearing Upper Plinth	2	07-Jul-17	08-Jul-17														P39/F4B - Install Pier Segment - Grouting			
	1032-2640	P39/F4B - Install Pier Segment - Stressing Nailing	2	10-Jul-17	11-Jul-17														P39/F4B - Install Pier Segment - Stressing			
	1032-2660	P39/F4B - Install MS at P39/F4B	2	12-Jul-17	13-Jul-17														P39/F4B - Install MS at P39/F4B			
	1032-2680	P39/F4B - Install Pier Segment - Relocate MS at P40/F5B to left and Engage FL at P39/F3B	2	14-Jul-17	15-Jul-17														P39/F4B - Install Pier Segment - Relocate			
	1032-2700	P39/F4B - T Span Erection (6 pairs)	4	17-Jul-17	20-Jul-17														P39/F4B - T Span Erection (6 pairs)			
All Middle Bridge F (Common)																						
	1032-4350	TCSS/LV Ducts at Pier 50-51	14	27-Apr-17	13-May-17			TCSS/LV Ducts at Pier 50-51														
	1032-4353	TCSS/LV Ducts at Pier 51-52	14	15-May-17	31-May-17				TCSS/LV Ducts at Pier 51-52													
	1032-4354	TCSS/LV Ducts at Pier 52-53	14	01-Jun-17	16-Jun-17					TCSS/LV Ducts at Pier 52-53												
	1032-4355	TCSS/LV Ducts at Pier 53-54	14	17-Jun-17	04-Jul-17						TCSS/LV Ducts at Pier 53-54											
	1032-4356	TCSS/LV Ducts at Pier 55-56	14	05-Jul-17	20-Jul-17							TCSS/LV Ducts at Pier 55-56										
10.4 - Bridge Deck Demolition																						
10.4.3 - Existing E/B Bridge																						
	10412-1650	Demolish Dolphin + Tie Beam & Reconstruct Tie Beam Pier 34	20	19-Jun-17	12-Jul-17										Demolish Dolphin + Tie Beam & Reconstruct Tie Beam Pier 34							
	10412-1670	Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 34 & 35 by Crane	9	08-Jun-17	17-Jun-17									Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 34 & 35 by Crane								
	10412-1700	Demolish Dolphin+Pile Cap & Reconstruct Pier 33 Pile Cap	20	19-Jun-17	12-Jul-17										Demolish Dolphin+Pile Cap & Reconstruct Pier 33 Pile Cap							
	10412-1710	Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 33	9	27-May-17	07-Jun-17							Demolish Temp. E/B Bridge - Crosshead & Pier > Pier 33										
	10412-1720	Demolish Temp. E/B Bridge - Deck > Pier 33 to 34 (6 beams)	5	22-May-17	26-May-17						Demolish Temp. E/B Bridge - Deck > Pier 33 to 34 (6 beams)											
	10412-1730	Demolish Dolphin+Pile Cap & Reconstruct Pier 32 Pile Cap	20	08-Jun-17	30-Jun-17									Demolish Dolphin+Pile Cap & Reconstruct Pier 32 Pile Cap								
	10412-1760	Demolish Dolphin+Pile Cap & Reconstruct Pier 31 Pile Cap	20	08-Mar-17 A	13-May-17		Demolish Dolphin+Pile Cap & Reconstruct Pier 31 Pile Cap															
	10412-1790	Demolish Dolphin+Pile Cap & Reconstruct Pier 30 Pile Cap	20	02-Mar-17 A	13-May-17		Demolish Dolphin+Pile Cap & Reconstruct Pier 30 Pile Cap															
	A3430	Demolish Pier + Steel Support at Pier 36	9	20-Apr-17 A	29-Apr-17		Demolish Pier + Steel Support at Pier 36															
	A3440	Launch LG-BM to next Bridge Span	1	02-May-17	02-May-17			Launch LG-BM to next Bridge Span														
	A3450	Demolish Four(4nos) Beams at Pier 35-34 - by LG-BM	2	03-May-17	04-May-17			Demolish Four(4nos) Beams at Pier 35-34 - by LG-BM														
	A3460	Dismantle LGB	14	05-May-17	20-May-17			Dismantle LGB														
10.5 - Temporary Bridge																						
10.5.2 - Temporary Bridge 'TB'																						

Activity ID		Activity Name	Rem Dur	Start	Finish	2017															
						May						June				July					
						16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
1052-1260	TB > Demolition of Temporary Bridge "TB"		4	03-Apr-17 A	24-Apr-17	TB > Demolition of Temporary Bridge "TB"															
10.6 - Tunnel Approach Ramp																					
10.6.1 - Approach Ramp (Excluding Portion IIB)																					
Piling Works																					
1061-3490	Moving Temp Car Park to Permanent Car Park Completed		0		27-Apr-17	◆ Moving Temp Car Park to Permanent Car Park Completed															
1061-3500	Pre Bored H-Pile > Pile Ramp - BM03 A		4	27-Apr-17	02-May-17	Pre Bored H-Pile > Pile Ramp - BM03 A															
1061-3520	Pre Bored H-Pile > Pile Ramp - BM03 A - (H-Pile + Grouting)		1	03-May-17	03-May-17	Pre Bored H-Pile > Pile Ramp - BM03 A - (H-Pile + Grouting)															
1061-3540	Pre Bored H-Pile > Pile Ramp - BM03 B		4	03-May-17	06-May-17	Pre Bored H-Pile > Pile Ramp - BM03 B															
1061-3560	Pre Bored H-Pile > Pile Ramp - BM03 B - (H-Pile + Grouting)		1	08-May-17	08-May-17	Pre Bored H-Pile > Pile Ramp - BM03 B - (H-Pile + Grouting)															
1061-3820	Pre Bored H-Pile > Pile Ramp - BN11 A(Low Head Rm)		8	08-May-17	16-May-17	Pre Bored H-Pile > Pile Ramp - BN11 A(Low Head Rm)															
1061-3840	Pre Bored H-Pile > Pile Ramp - BN11 A - (H-Pile + Grouting)		1	17-May-17	17-May-17	Pre Bored H-Pile > Pile Ramp - BN11 A - (H-Pile + Grouting)															
1061-3860	Pre Bored H-Pile > Pile Ramp - BN11 B (LHR)		8	08-May-17	16-May-17	Pre Bored H-Pile > Pile Ramp - BN11 B (LHR)															
1061-3880	Pre Bored H-Pile > Pile Ramp - BN11 B - (H-Pile + Grouting)		1	17-May-17	17-May-17	Pre Bored H-Pile > Pile Ramp - BN11 B - (H-Pile + Grouting)															
1061-3900	Pre Bored H-Pile > Pile Ramp - BN12 A (LHR)		8	17-May-17	25-May-17	Pre Bored H-Pile > Pile Ramp - BN12 A (LHR)															
1061-3920	Pre Bored H-Pile > Pile Ramp - BN12 A - (H-Pile + Grouting)		1	26-May-17	26-May-17	Pre Bored H-Pile > Pile Ramp - BN12 A - (H-Pile + Grouting)															
1061-3940	Pre Bored H-Pile > Pile Ramp - BN12 B (LHR)		8	17-May-17	25-May-17	Pre Bored H-Pile > Pile Ramp - BN12 B (LHR)															
1061-3960	Pre Bored H-Pile > Pile Ramp - BN12 B - (H-Pile + Grouting)		1	26-May-17	26-May-17	Pre Bored H-Pile > Pile Ramp - BN12 B - (H-Pile + Grouting)															
1061-3980	Pre Bored H-Pile > Pile Ramp - BN13 A (LHR)		8	26-May-17	05-Jun-17	Pre Bored H-Pile > Pile Ramp - BN13 A (LHR)															
1061-4000	Pre Bored H-Pile > Pile Ramp - BN13 A - (H-Pile + Grouting)		1	06-Jun-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BN13 A - (H-Pile + Grouting)															
1061-4020	Pre Bored H-Pile > Pile Ramp - BN13 B (LHR)		8	26-May-17	05-Jun-17	Pre Bored H-Pile > Pile Ramp - BN13 B (LHR)															
1061-4040	Pre Bored H-Pile > Pile Ramp - BN13 B - (H-Pile + Grouting)		1	06-Jun-17	06-Jun-17	Pre Bored H-Pile > Pile Ramp - BN13 B - (H-Pile + Grouting)															
1061-4060	Pre Bored H-Pile > Pile Ramp - BN01 A (LHR)		8	06-Jun-17	14-Jun-17	Pre Bored H-Pile > Pile Ramp - BN01 A (LHR)															
1061-4080	Pre Bored H-Pile > Pile Ramp - BN01 A - (H-Pile + Grouting)		1	15-Jun-17	15-Jun-17	Pre Bored H-Pile > Pile Ramp - BN01 A - (H-Pile + Grouting)															
1061-4100	Pre Bored H-Pile > Pile Ramp - BN01 B (LHR)		8	06-Jun-17	14-Jun-17	Pre Bored H-Pile > Pile Ramp - BN01 B (LHR)															
1061-4120	Pre Bored H-Pile > Pile Ramp - BN01 B - (H-Pile + Grouting)		1	15-Jun-17	15-Jun-17	Pre Bored H-Pile > Pile Ramp - BN01 B - (H-Pile + Grouting)															
1061-4140	Pre Bored H-Pile > Pile Ramp - BN05 A (LHR)		8	15-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BN05 A (LHR)															
1061-4160	Pre Bored H-Pile > Pile Ramp - BN05 A - (H-Pile + Grouting)		1	24-Jun-17	24-Jun-17	Pre Bored H-Pile > Pile Ramp - BN05 A - (H-Pile + Grouting)															
1061-4180	Pre Bored H-Pile > Pile Ramp - BN05 B (LHR)		8	15-Jun-17	23-Jun-17	Pre Bored H-Pile > Pile Ramp - BN05 B (LHR)															
1061-4200	Pre Bored H-Pile > Pile Ramp - BN05 B - (H-Pile + Grouting)		1	24-Jun-17	24-Jun-17	Pre Bored H-Pile > Pile Ramp - BN05 B - (H-Pile + Grouting)															
1061-4220	Pre Bored H-Pile > Pile Ramp - BN06 A (LHR)		8	24-Jun-17	04-Jul-17	Pre Bored H-Pile > Pile Ramp - BN06 A (LHR)															
1061-4240	Pre Bored H-Pile > Pile Ramp - BN06 A - (H-Pile + Grouting)		1	05-Jul-17	05-Jul-17	Pre Bored H-Pile > Pile Ramp - BN06 A - (H-Pile + Grouting)															
1061-4260	Pre Bored H-Pile > Pile Ramp - BN06 B (LHR)		8	24-Jun-17	04-Jul-17	Pre Bored H-Pile > Pile Ramp - BN06 B (LHR)															
1061-4280	Pre Bored H-Pile > Pile Ramp - BN06 B - (H-Pile + Grouting)		1	05-Jul-17	05-Jul-17	Pre Bored H-Pile > Pile Ramp - BN06 B - (H-Pile + Grouting)															
1061-4300	Remaining Bored Piles & Pre-Bored H-Pile Testing		30	31-May-17	05-Jul-17	Remaining Bored Piles & Pre-Bored H-Pile Testing															
Excavation & ELS Works																					

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work


Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 April 2017 to 19 July 2017)

Page 6 of 9

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																														
							May				June				July																				
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23																
1061-4901.2	Sheet Piling Works (WF1>B3:19m@1.5m/d) (incl Re-boring & Welding Remedial Works)	9	12-Jul-16 A	29-Apr-17			Sheet Piling Works (WF1>B3:19m@1.5m/d) (incl Re-boring & Welding Remedial Works)																												
1061-4910	Advance Sheet Piling Works + Pre-drilling in Phase 2 - Cul de sac Area (30m)	14	04-Apr-17 A	17-May-17				Advance Sheet Piling Works + Pre-drilling in Phase 2 - Cul de sac Area (30m)																											
1061-4915	Tam Grouting	12	14-Sep-16 A	04-May-17			Tam Grouting																												
1061-5060	Dewatering Well Installation (14Nos)	9	11-Jan-17 A	29-Apr-17			Dewatering Well Installation (14Nos)																												
1061-5080	Observation Well Installation (10Nos)	9	13-Feb-17 A	29-Apr-17			Observation Well Installation (10Nos)																												
1061-5100	Pumping Test	9	05-May-17	15-May-17				Pumping Test																											
1061-5120	Complete Pump Test	0		15-May-17				◆ Complete Pump Test																											
1061-5140	Ch 5285 - 5331 > Excav from Ex. Lvl down to 2.5mPD (Ch 5285 - 5331 w/ open cut)	7	15-Aug-16 A	27-Apr-17			Ch 5285 - 5331 > Excav from Ex. Lvl down to 2.5mPD (Ch 5285 - 5331 w/ open cut)																												
1061-5160	Ch 5234 - 5285 > Excav from Ex. Lvl down to 2.5mPD	9	30-Mar-17 A	09-May-17			Ch 5234 - 5285 > Excav from Ex. Lvl down to 2.5mPD																												
1061-5180	Ch 5234 - 5285 > Install 1st Layer of Strut & Waling	9	10-May-17	19-May-17				Ch 5234 - 5285> Install 1st Layer of Strut & Waling																											
1061-5200	Ch 5234 - 5285 > Excav from 2.5mPD to 1m Below 2nd Layer of Struts	16	20-May-17	08-Jun-17				Ch 5234 - 5285 > Excav from 2.5mPD to 1m Below 2nd Layer of Struts																											
1061-5220	Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling	9	09-Jun-17	19-Jun-17					Ch 5234 - 5285 > Install 2nd Layer of Strut & Waling																										
1061-5240	Ch 5234 - 5285 > Excav to FEL	13	20-Jun-17	05-Jul-17						Ch 5234 - 5285 > Excav to FEL																									
Structure Works																																			
1061-5260	Bay 1 - Ch 5322 - 5331 > Base Slab - Blinding Layer	1	09-Jun-17	09-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Blinding Layer																					
1061-5280	Bay 1 - Ch 5322 - 5331 > Base Slab - Water Proofing Membrane	2	10-Jun-17	12-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Water Proofing Membrane																					
1061-5300	Bay 1 - Ch 5322 - 5331 > Base Slab - Rebar Fixing	5	13-Jun-17	17-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Rebar Fixing																					
1061-5320	Bay 1 - Ch 5322 - 5331 > Base Slab - Erect Formworks	4	19-Jun-17	22-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Erect Formwo																					
1061-5340	Bay 1 - Ch 5322 - 5331 > Base Slab - Concreting	1	23-Jun-17	23-Jun-17										Bay 1 - Ch 5322 - 5331 > Base Slab - Concreting																					
1061-5360	Bay 2 - Ch 5313 - 5322 > Base Slab - Blinding Layer	1	24-Jun-17	24-Jun-17										Bay 2 - Ch 5313 - 5322 > Base Slab - Blinding Lay																					
1061-5380	Bay 2 - Ch 5313 - 5322 > Base Slab - Water Proofing Membrane	2	26-Jun-17	27-Jun-17										Bay 2 - Ch 5313 - 5322 > Base Slab - Water P																					
1061-5400	Bay 2 - Ch 5313 - 5322 > Base Slab - Rebar Fixing	5	28-Jun-17	04-Jul-17										Bay 2 - Ch 5313 - 5322 > Base Slab																					
1061-5420	Bay 2 - Ch 5313 - 5322 > Base Slab - Erect Formworks	4	05-Jul-17	08-Jul-17										Bay 2 - Ch 5313 - 5322 > Bas																					
1061-5440	Bay 2 - Ch 5313 - 5322 > Base Slab - Concreting	1	10-Jul-17	10-Jul-17										Bay 2 - Ch 5313 - 5322 > B																					
1061-5460	Bay 3 - Ch 5303 - 5313 > Base Slab - Blinding Layer	1	11-Jul-17	11-Jul-17										Bay 3 - Ch 5303 - 5313 >																					
1061-5480	Bay 3 - Ch 5303 - 5313 > Base Slab - Water Proofing Membrane	2	12-Jul-17	13-Jul-17										Bay 3 - Ch 5303 - 531																					
1061-5500	Bay 3 - Ch 5303 - 5313 > Base Slab - Rebar Fixing	5	14-Jul-17	19-Jul-17										Bay 3 - Ch 53																					
1061-5560	Bay 6 - Ch 5262 - 5277 > Base Slab - Blinding Layer	1	06-Jul-17	06-Jul-17										Bay 6 - Ch 5262 - 5277 > Base S																					
1061-5580	Bay 6 - Ch 5262 - 5277 > Base Slab - Water Proofing Membrane	2	07-Jul-17	08-Jul-17										Bay 6 - Ch 5262 - 5277 > Bas																					
1061-5600	Bay 6 - Ch 5262 - 5277 > Base Slab - Rebar Fixing	6	10-Jul-17	15-Jul-17										Bay 6 - Ch 5262 - 5																					
Retaining Walls & Trough Structure B,C & D																																			
1061-6860	Construct Retaining Wal E Pile Cap (7 nos)	24	06-Mar-17 A	18-May-17			Construct Retaining Wal E Pile Cap (7 nos)																												
1061-6880	Construct Retaining Wal E1 (Ch 5332 - 5371)	18	19-May-17	09-Jun-17					Construct Retaining Wal E1 (Ch 5332 - 5371)																										
1061-6900	Construct Retaining Wal E3 (Ch 5371 - 5398)	18	10-Jun-17	30-Jun-17						Construct Retaining Wal E3 (Ch 5371 - 5																									
1061-6920	Construct Retaining Wal E3 (Ch 5398 - 5419)	18	19-May-17	09-Jun-17					Construct Retaining Wal E3 (Ch 5398 - 5419)																										
Remaining Level of Effort		Remaining Work		Contract HY/2009/19 Three Months Rolling Programme (20 April 2017 to 19 July 2017)																															
Actual Level of Effort		Critical Remaining Work																																	
Actual Work		Milestone																																	
Page 7 of 9																																			

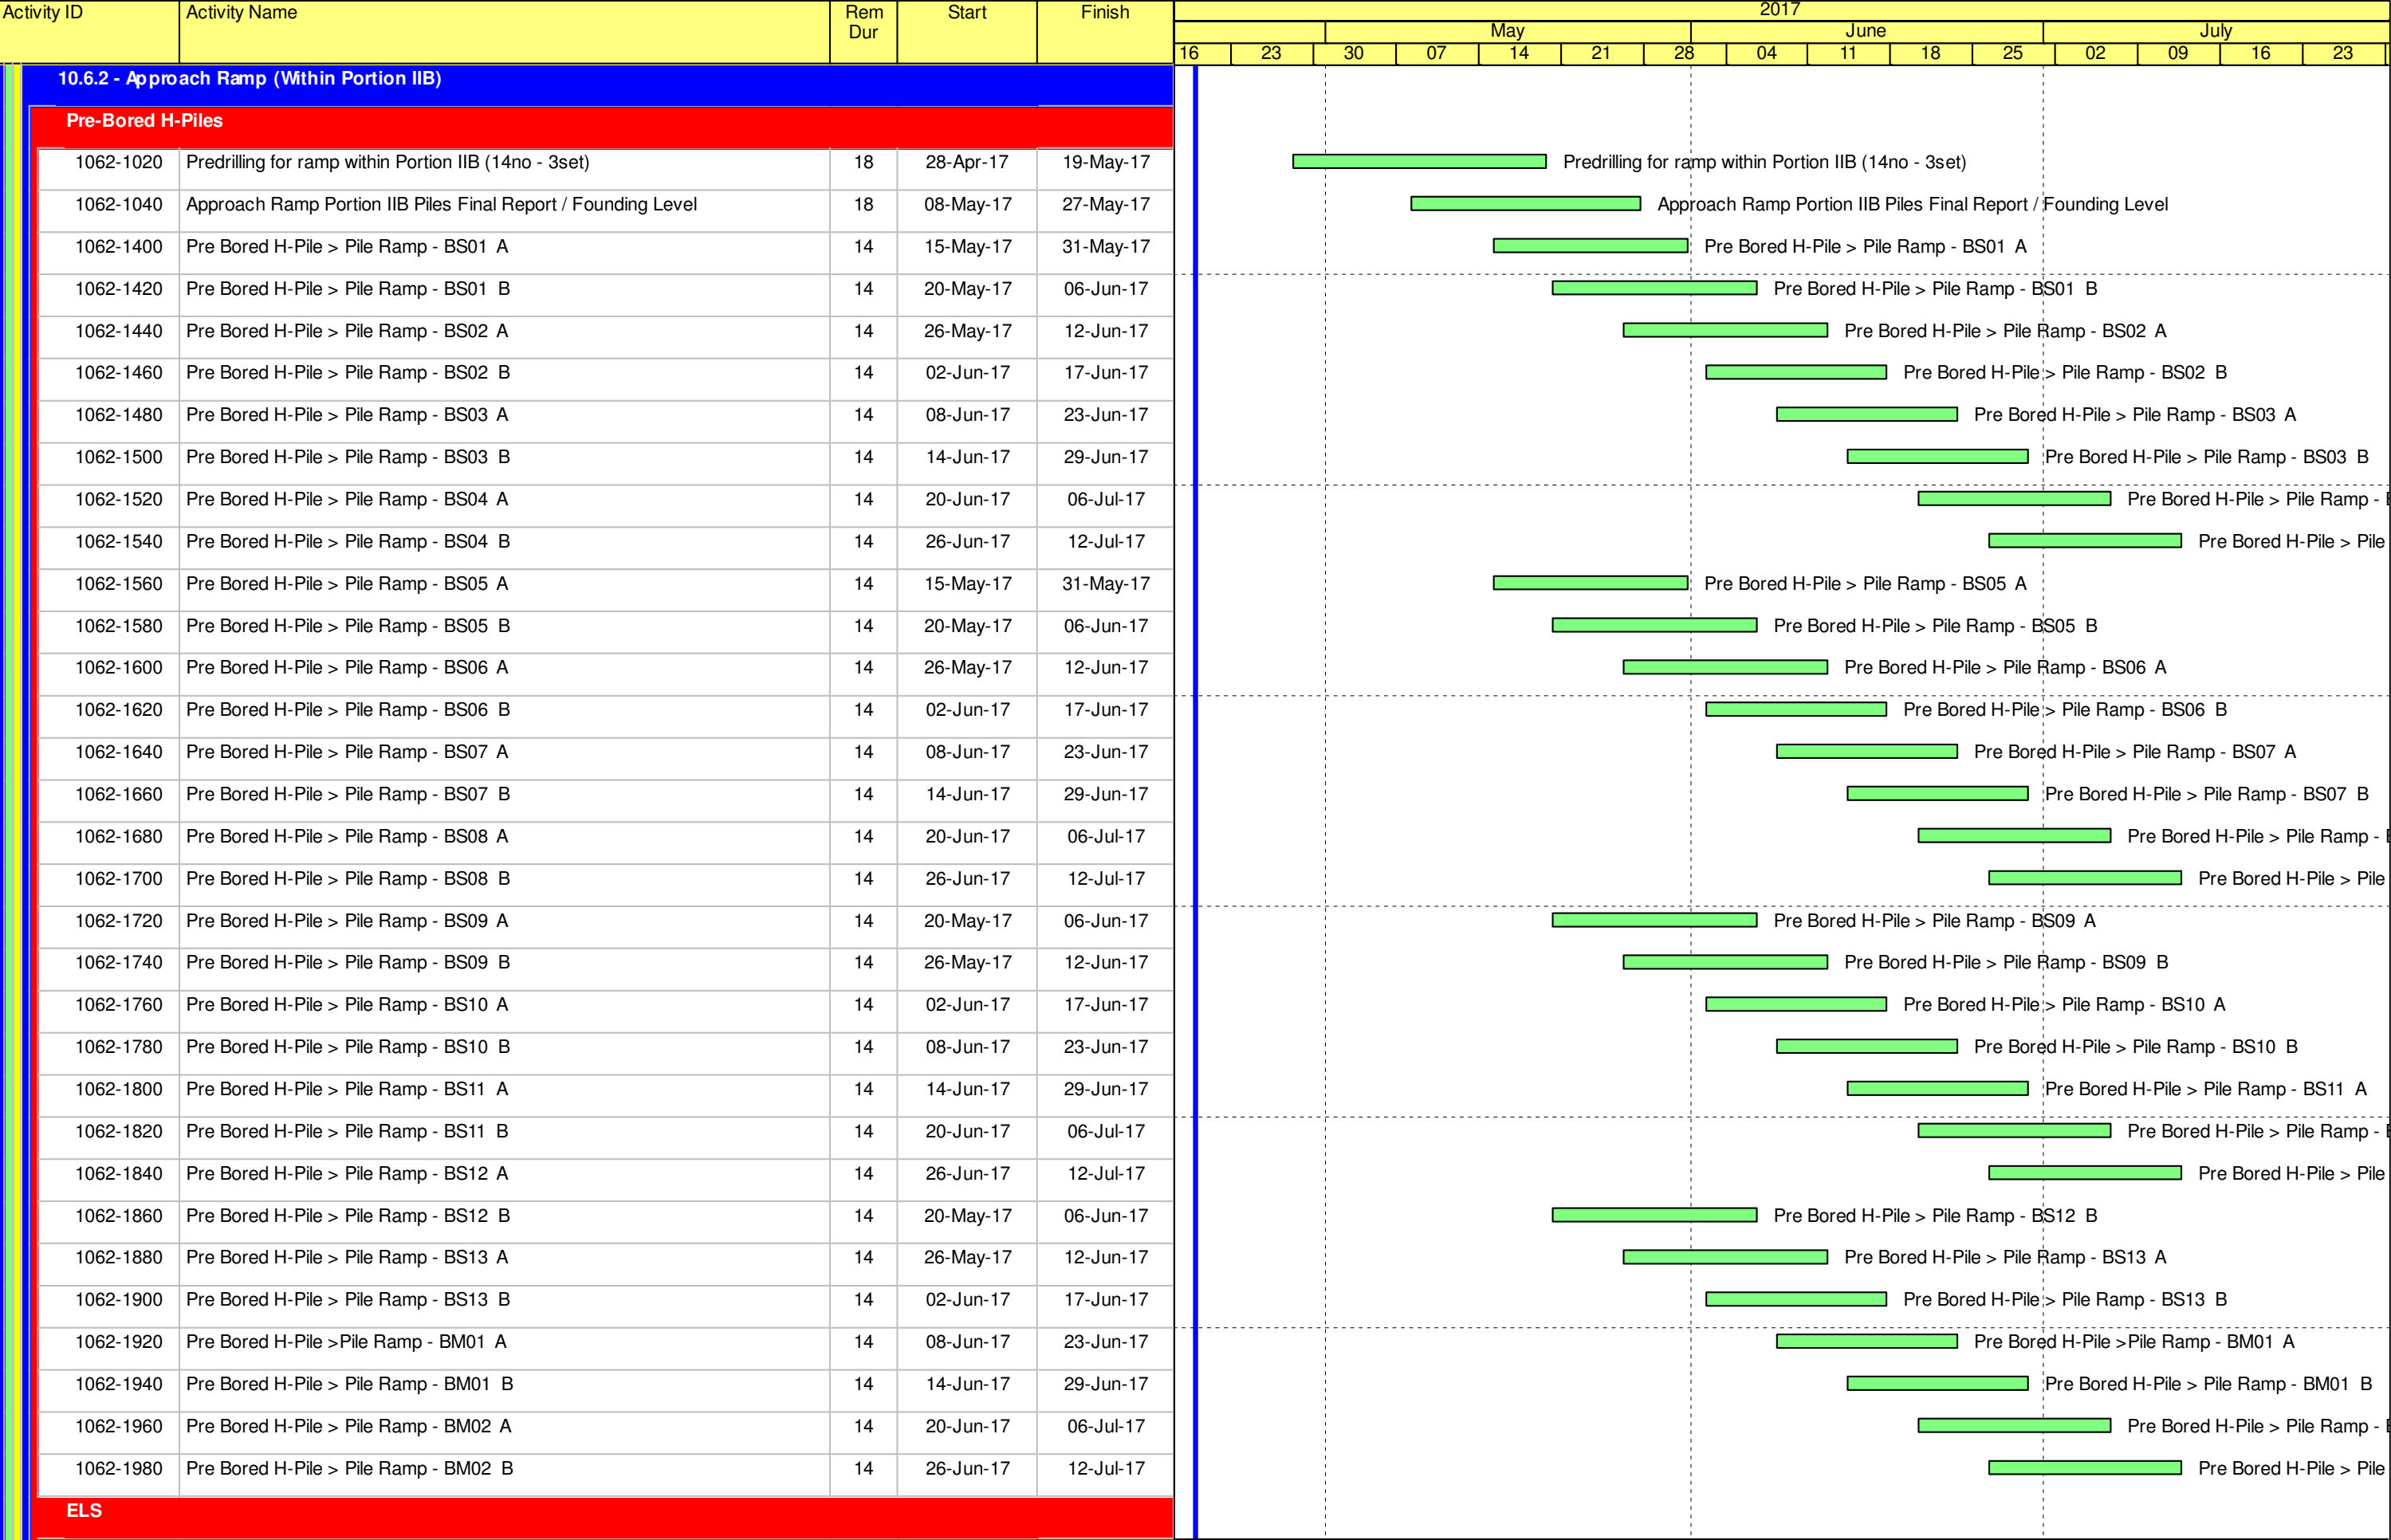

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Milestone

Activity ID	Activity Name	Rem Dur	Start	Finish	2017																
									May				June				July				
					16	23	30	07	14	21	28	04	11	18	25	02	09	16	23		
	A1000	Sheet Pile and Preboring Works	61	09-May-17	20-Jul-17	Sheet Pile and Preboring Works															
	A1010	Dewatering System and Instrumentation installation	38	31-May-17	14-Jul-17	Dewatering System and Instrumentation installation															
10.7 - Section X - Miscellaneous Works																					
10.7.2 - Oil Street/Watson Road (Portion III)																					
	1072-1000	Remaining Fresh Water Main 200DI - F02 Portion VIIB (Watson/VB)	120	27-Apr-17	16-Sep-17	Remaining Fresh Water Main 200DI - F02 Portion VIIB (Watson/VB)															
	1072-1020	Remaining Storm Water Drain Portion VII (Watson/VB)	120	27-Apr-17	16-Sep-17	Remaining Storm Water Drain Portion VII (Watson/VB)															
	1072-1040	Fresh Water Main 100DI - F03 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Fresh Water Main 100DI - F03 Portion III (Oil Street/Admin Bldg)															
	1072-1060	Salt Water Main 100DI - S03 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Salt Water Main 100DI - S03 Portion III (Oil Street/Admin Bldg)															
	1072-1065	Salt Water Main 100DI - S02 (Watson rd - Previously at Portion XIIB)	50	27-Apr-17	26-Jun-17	Salt Water Main 100DI - S02 (Watson rd - Previously at Portion XIIB)															
	1072-1080	Foul Sewer Dia. 225 Portion III (Oil Street/Admin Bldg)	50	27-Apr-17	26-Jun-17	Foul Sewer Dia. 225 Portion III (Oil Street/Admin Bldg)															
10.7.3 - Open Area																					
	1073-1010	Open Area - Pedestrian Parapet -Ch570.40 to Ch540.00	14	22-May-17*	07-Jun-17	Open Area - Pedestrian Parapet -Ch570.40 to Ch540.00															
	1073-1010.3	Open Area - Pedestrian Parapet - Ch540.00 to Ch520.00	14	08-Jun-17	23-Jun-17	Open Area - Pedestrian Parapet - Ch540.00 to Ch520.00															
	1073-1010.5	Open Area - Pedestrian Parapet - Ch0.00 - Ch40.00	14	24-Jun-17	11-Jul-17	Open Area - Pedestrian Parapet - Ch0.00 - Ch40.00															
	1073-1010.7	Open Area - Pedestrian Parapet - Ch40.00 - 80.00	14	12-Jul-17	27-Jul-17	Open Area - Pedestrian Parapet - Ch40.00 - 80.00															
11 - SECTION 11 OF THE WORKS																					
11.1 - Portion XIIA - Stage 1																					
11.1.1 - Along Watson Road - Waterwork & Roadworks (Portion XIIA)																					
	1110-2820	Permanent Cul-de Sac - Constr. of drainage	25	20-Apr-17*	19-May-17	Permanent Cul-de Sac - Constr. of drainage															
	1110-2830	Permanent Cul-de Sac - Constr. of watermains	25	03-May-17	01-Jun-17	Permanent Cul-de Sac - Constr. of watermains															
	1110-2840	Permanent Cul-de Sac - Constr. of public lighting & telecom (conduits & drawpits)	25	15-May-17	13-Jun-17	Permanent Cul-de Sac - Constr. of public lighting & telecom (conduits & drawpits)															
	1110-2850	Permanent Cul-de Sac - Constr. of (kerbs & pavements)	25	14-Jun-17	13-Jul-17	Permanent Cul-de Sac - Constr. of (kerbs & pavements)															
11.1.3 - Along Tsing Fung St. - TCSS cable ducting (Portion XIIA)																					
	1110-2930	TCSS cable ducting along Tsing Fung St	36	08-May-17*	19-Jun-17	TCSS cable ducting along Tsing Fung St															
11.1.4 - Along Gordon House - Cross road ducting at Hing Fat St adjacent to (Portion XIIA)																					
	1110-2940	Trench 1 (E&M, PL) - (Night Work)	16	19-Sep-16 A	09-May-17	Trench 1 (E&M, PL) - (Night Work)															
	1110-2950	Trench 2 (ATC) - (Night Work)	38	10-May-17	23-Jun-17	Trench 2 (ATC) - (Night Work)															
11.1.5 - Footing and frame/pole for directional sign FVMSh2, ADS16 and OHVD (Portion XIIA)																					
	1110-2960	ADS16	26	14-Sep-16 A	20-May-17	ADS16															
	1110-2970	OHVD	12	22-May-17	05-Jun-17	OHVD															
	1110-2980	FVMSh2	18	06-Jun-17	26-Jun-17	FVMSh2															

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone
