The Hong Kong Jockey Club

2008 Olympic Equestrian Event

Monthly Environmental Monitoring and Audit Report - September 2007

**Final** 

The Hong Kong Jockey Club

# 2008 Olympic Equestrian Event

Monthly Environmental Monitoring and Audit Report – September 2007

October 2007

18-OCT-2007 17:33



# INDEPENDENT ENVIRONMENTAL CHECKER CHECK CERTIFICATE

Independent Environmental Checker for Main Arcna of the 2008 Olympic Equestrian Event Monthly EM&A Report for September 2007 (Final)

We confirm having used reasonable skill and care in the preparation of the Monthly EM&A Report and we certify that we can verify the report.

Signed:

Independent Environmental Checker

H. J. Cochrane Director and IEC

Date:

(8 October 2007



Page 1 of 1

ARUP

| Job title      |          | 2008 Olympic Equestrian Event   |                  |               | Job number                    |  |
|----------------|----------|---|------------------|---------------|-------------------------------|--|
|                |          |   | 24469            |               |                               |  |
| Document title |          | Monthly Environmental Monitoring and Audit Report - September 2007 File reference |                  |               |                               |  |
| Revision       | Date     | Filename  | 14-SEP-07.doc    |               |                               |  |
| Final          | 23/10/07 | Description   | Final submission |               |                               |  |
|                |          |   |                  |               |                               |  |
|                |          |   | Prepared by      | Checked by    | Approved by                   |  |
|                |          | Name  | Fanny Wong       | Sam Tsoi      | Sam Tsoi                      |  |
|                |          | Signature   | Janz             |               |                               |  |
|                |          | Filename  | () 0             |               |                               |  |
|                |          | Description   |                  |               |                               |  |
|                |          |   | Prepared by      | Checked by    | Approved by                   |  |
|                |          | Name  |                  |               |                               |  |
|                |          | Signature   |                  |               |                               |  |
|                |          | Filename  |                  |               |                               |  |
|                |          | Description   |                  |               |                               |  |
|                |          |   | Prepared by      | Checked by    | Approved by                   |  |
|                |          | Name  |                  |               |                               |  |
|                |          | Signature   |                  |               |                               |  |
|                |          | Filename  |                  |               |                               |  |
|                |          | Description   |                  |               |                               |  |
|                |          |   | Prepared by      | Checked by    | Approved by                   |  |
|                |          | Name  |                  |               |                               |  |
|                |          | Signature   |                  |               |                               |  |
|                |          | I.  |                  | Issue Documer | nt Verification with Document |  |
|                |          |   |                  |               |                               |  |

# **Contents**

| Exec | cutive Sun | nmary   | Page<br>i          |
|------|------------|---|--------------------|
| 1    | Introdu    | uction  | 1                  |
|      | 1.1        | Project Background  | 1                  |
|      | 1.2        | Project Organisation  | 2                  |
|      | 1.3        | Scope of Impact EM&A  | 2                  |
|      | 1.4        | Purpose of the Report   | 2                  |
| 2    | Scope      | e of Construction Works   | 2                  |
|      | 2.1        | Construction Programme  | 2                  |
|      | 2.2        | Construction Activities of the Month  | 2                  |
| 3    | Summ       | nary of EM&A Requirements   | 3                  |
|      | 3.1        | Construction Noise  | 3                  |
|      | 3.2        | Landscape and Visual  | 4                  |
|      | 3.3        | Performance Limits and Event-Action Plans   | 4                  |
|      | 3.4        | Site Inspection and Environmental Complaint Handling                                | 5                  |
|      | 3.5        | Environmental Mitigation Measures   | 7                  |
| 4    | Noise      | Monitoring  | 9                  |
|      | 4.1        | Monitoring Equipment  | 9                  |
|      | 4.2        | Methodology   | 9                  |
|      | 4.3        | Results and Observations  | 9                  |
| 5    | Lands      | cape and Visual Monitoring and Audit  | 10                 |
|      | 5.1        | Summary of Inspection   | 10                 |
|      | 5.2        | Audit Schedule  | 10                 |
| 6    |            | spection, Waste Disposal, Environmental Complaints, Environmental ompliance Records | Licenses and<br>11 |
|      | 6.1        | Site Audit Findings   | 11                 |
|      | 6.2        | Waste Disposal  | 11                 |
|      | 6.3        | Complaint Record  | 11                 |
|      | 6.4        | Exceedance  | 12                 |
|      | 6.5        | Notification of Summons and Successful Prosecution                                  | 12                 |
|      | 6.6        | Environmental Licenses  | 12                 |
| 7    | Future     | e Key Issue   | 12                 |
|      | 7.1        | Forecast of Works Programme   | 12                 |
|      | 7.2        | Key Issues for Coming Month   | 12                 |
| 8    | Comm       | nents, Recommendations and Conclusion   | 12                 |
|      | 8.1        | Comments and Recommendations  | 12                 |
|      | 8.2        | Conclusion  | 13                 |

9 References 13

## **Appendices**

Appendix A

Construction Programme

(Construction Work has been Completed)

Appendix B

Monitoring Schedule for September and October 2007

Appendix C

Environmental Mitigation Implementation Schedule

Appendix D

Calibration certificates of noise monitoring equipment

Appendix E

Detailed noise monitoring results

Appendix F

Landscape and visual monitoring and audit report

Appendix G

Log records and details of environmental complaints

G:\...\2007-09\14-SEP-07.DOC

# **Executive Summary**

This is the fourteenth monthly environmental monitoring and audit (EM&A) report presenting the progress of environmental monitoring and audit work for Main Arena of the 2008 Olympic Equestrian Event for the period from 1 to 30 September 2007, including noise monitoring and landscape and visual audit. Noise was measured in terms of  $L_{eq(30min)}$  with  $L_{10}$  and  $L_{90}$  measurements for reference.

A total of 4 sets of daytime (0700 – 1900 hours) noise monitoring was conducted on 7, 13, 19 and 29 September 2007. The highest noise level of 64.5 dB(A) was recorded at the roof of Racecourse Villa (NM2) on 7 September 2007 while the lowest noise level of 60.8 dB(A) was recorded at the podium outside Block 1 of Ravana Garden (NM3) on 13 September 2007. There was no exceedance of noise A/L Levels recorded during the reporting period.

A total of 2 landscape and visual audits were carried out bi-weekly on 10 and 18 September 2007. The Registered Landscape Architect (RLA) has the following observations:

- Stables have been constructed. Planting Work has been completed. Transplanted trees and planted trees are generally in fair condition.
- The Contractor shall remove all wild climbers growing on transplanted trees and remove dead branches of retained trees.

A total of 4 environmental site audits were conducted weekly on 4, 13, 17 and 24 September 2007. No major issues of environmental concern were observed.

No C&D waste and C&D material was generated in September 2007. No chemical waste was disposed of during the reporting period.

No environmental complaint was received during the reporting period.

No new construction noise permit was granted during the reporting period.

No exceedance of noise monitoring action/limit levels was recorded during the reporting period.

There was neither notification of summons nor prosecution received during the reporting period.

#### 1 Introduction

#### 1.1 Project Background

Having considered the advantage of established international equine import and export protocols as well as the supporting facilities already in place, the International Olympic Committee (IOC) has accepted the Beijing Organising Committee for the Games of the 29<sup>th</sup> Olympiad (BOCOG)'s proposal of staging the 2008 Olympic and Paralympic Equestrian Events in Hong Kong.


Given the very tight schedule of the project, Hong Kong Sports Institute (HKSI) in Shatin will be temporarily converted into the core competition venues for the Olympic Equestrian Event. Facilities to be provided on the core venues include:

- Main Competition Arena for 20,000 spectators
- Stable Complex
- Training Arenas
- Logistic Compound
- Spectator Entry & Broadcast Compound
- Food & Merchandise

The venues will be in operation for approximately one month during the Olympic event, with the competition expected to last from between 10 to 14 days. 14 days after the Olympic Events, the Paralympic competition will be staged, which will last for a few days.

One year before the 2008 Olympic Event, the site will be occupied for the Test Event, which is used by all divisions of the Olympic Organising Committee to test their organisational capabilities for the Games and Event Management to trail the equine facilities and the footing (riding surface) of the Main Arena, Stables and Training Facilities. These mock up events are known as the 'Test Event Mode', and limited public access will be given.

Figure 1-1: Location plan of the project

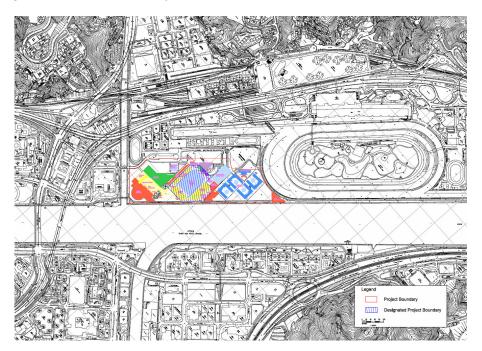

The implementation of the Project is scheduled from July 2006 to December 2008. Table 1-1 gives the tentative project timetable and phasing.

Table 1-1: Timetable and phasing for the Project

| Task                         | Start                   | Finish        |
|------------------------------|-------------------------|---------------|
| Pre- Test Event Construction | July 2006               | June 2007     |
| Test Event                   | August 2007 (2 weeks)   |               |
| Post Test Event Construction | September 2007          | June 2008     |
| Olympic Event                | August 2008 (2 weeks)   |               |
| Paralympic Event             | September 2008 (1 week) |               |
| Reinstatement of HKSI        | October 2008            | December 2008 |

The Main Arena of the 2008 Olympic Equestrian Event is classified as a Designated Project (DP) under item O7, Part 1, Schedule 2 of the Environmental Impact Assessment Ordinance (EIAO) – an outdoor sporting facility with a capacity to accommodate more than 10,000 persons.

In accordance with the requirements of Section 5(1) of the EIAO, a project profile (No. PP-266/2005) was submitted to Environmental Protection Department (EPD) for the application of an EIA Study Brief on 17 October 2005. Pursuant to Section 5(7)(a) of the EIAO, EPD issued to The Hong Kong Jockey Club (HKJC) a study brief (ref: EIA Study Brief No: ESB-136/2005 dated 7 November 2005) to carry out an EIA study.

The EIA Report for the Project (EIA-118/2005) was approved and an Environmental Permit (EP) (EP-236/2006) granted by EPD on 24<sup>th</sup> and 25<sup>th</sup> March 2006 respectively.

#### 1.2 Project Organisation

The Project Proponent is the Hong Kong Jockey Club (HKJC); the Engineer's Representative (ER) is Ove Arup & Partners Hong Kong Ltd (Arup); the Contractor is China State Construction Engrg (HK) Ltd; the Independent Environmental Checker (IEC) is Meinhardt Infrastructure and Environment Ltd; the Environmental Team (ET) is Arup.

#### 1.3 Scope of Impact EM&A

The impact environmental monitoring and audit for the Project included noise monitoring, landscape and visual audit, and environmental site audit.

#### 1.4 Purpose of the Report

The purpose of this monthly EM&A report is to provide information on monitoring methodology, monitoring results, environmental permit status, site audit findings, recommendations and conclusions of the EM&A of the project.

This is the fourteenth monthly EM&A report prepared by Arup for the submission to the HKJC summarising the implementation of the EM&A programme from 1 to 30 September 2007.

# **2** Scope of Construction Works

#### 2.1 Construction Programme

The construction works commenced on 15 August 2006. Pre-Test Event construction works was completed in mid July. No construction work was carried out during the reporting period. **Appendix A** shows the latest construction programmed provided by the Contractor.

#### 2.2 Construction Activities of the Month

There was no construction work carried out during the reporting period.

# 3 Summary of EM&A Requirements

Noise monitoring shall be conducted by the ET at specified monitoring locations during the construction stage. Landscape and visual audits and environmental site audits shall also carried out. The monitoring schedule for the month of September 2007 and the tentative schedule for October 2007 are attached in **Appendix B**.

#### 3.1 Construction Noise

#### 3.1.1 Monitoring Parameters

Construction noise is measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ).  $L_{10}$  and  $L_{90}$  were also recorded as supplementary reference information for data auditing.

#### 3.1.2 Monitoring Frequency

Noise monitoring was performed on a weekly basis in accordance with the EM&A Manual. The monitoring time periods, parameters and frequency are summarised in Table 3-1.

Table 3-1: Construction noise monitoring parameters and frequency

| Time Period (when construction activity is found) | Parameters  | Monitoring<br>Frequency | No. of Measurements for Each Monitoring |
|---|-------------|-------------------------|---|
| Between 0700-1900 hours on normal weekdays        | Leq(30 min) |                         | 1                                       |
| Between 1900-2300 hours on normal weekdays        |             | Once per                | 3 (consecutive)                         |
| Between 2300-0700 hours of next day               | Leq(5 min)* | week                    |   |
| Between 0700-1900 hours on holidays               |             |                         |   |

The L<sub>eq(5 min)</sub> will only be measured if construction activities are conducted during holidays and between the period of 1900 and 0700 hours during normal weekdays.

#### 3.1.3 Monitoring Locations

A total of three locations were specified for the noise monitoring as shown in Table 3-2 and Figure 3-1. Measurements were conducted at a position 1.2m above ground and kept away from reflective surface.

Table 3-2: Construction noise monitoring locations

| Monitoring<br>Station ID | Location                                   | Monitoring Point  |
|--------------------------|--|---|
| NM1                      | Chung Cheung Court,<br>HKJC Staff Quarters | On the roof, 1 meter from façade, facing the main works area                    |
| NM2                      | Racecourse Villa                           | On the roof, 1meter from façade, facing the main works area                     |
| NM3                      | Ravana Garden                              | On the podium outside Block 1, 1 meter from façade, facing the main works area. |

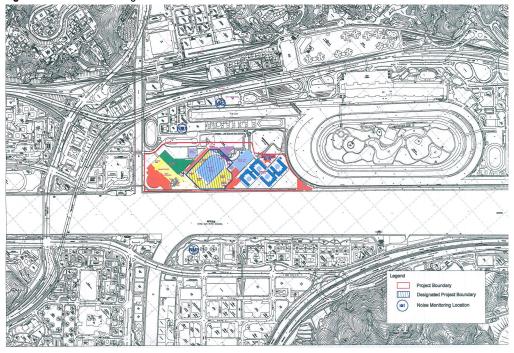


Figure 3-1: Noise Monitoring Location

#### 3.2 Landscape and Visual

#### 3.2.1 Audit Parameters

All landscape and visual mitigation measures implemented by both the Contractor Team (CT) and the Landscape Contractor during the construction phase and the first year of the operational phase shall be audited by a landscape auditor, to ensure compliance with the aims of the mitigation measures.

#### 3.2.2 Audit Frequency

The landscape and visual monitoring and audit shall be undertaken once every two weeks throughout the construction, operation and reinstatement phases.

#### 3.2.3 Audit Location

The landscape and visual monitoring and audit shall be conducted throughout the entire site area.

#### 3.3 Performance Limits and Event-Action Plans

The monitoring results will be checked against appropriate standards and requirements. A two-tier system performance limits have been established in the Project specific EM&A Manual. The "Action Level" and the "Limit Level" (A/L) are established according to the EPD requirements. The ET, ER, IEC, and CT will take corresponding action in accordance with the Event-Action Plans if the monitoring results exceed the performance limits.

#### 3.3.1 Construction Noise

The A/L Levels for construction noise have been established in accordance with TM-EIAO as summarised in Table 3-3.

Table 3-3: Action and Limit Levels for construction noise

| Time Period   | Action Level                              | Limit Level |
|---|---|-------------|
| 0700 – 1900 hours on any day not being a Sunday or public holiday | When one documented complaint is received | 75 dB(A)    |

The action required to be taken by different parties in the case of occurrence of exceedance of A/L Levels are summarised in the Event and Action Plan in Table 3-4.

Table 3-4: Event and Action Plan for construction noise exceedance

| Event           | Action   |   |  |   |  |  |
|-----------------|--|---|--|---|--|--|
| Event           | ET Leader  | IEC   | ER   | Contractor  |  |  |
| Action<br>Level | Notify IEC, ER and the Contractor within 24 hours of identification of the exceedance.     Carry out investigation.     Report the results of investigation to IEC, ER and the Contractor.     Discuss with the Contractor and formulate remedial measures.     Increase monitoring frequency to check mitigation measures.  | Review with analysed results submitted by ET.     Review the proposed remedial measures by the Contractor and advise ER accordingly.     Supervise the implementation of remedial measures.   | Confirm receipt of notification of exceedance in writing.     Notify the Contractor.     Require the Contractor to propose remedial measures for the analysed noise problem.     Ensure remedial measures are properly implemented.  | Submit noise mitigation proposals to ER and IEC.     Implement noise mitigation proposals.  |  |  |
| Limit<br>Level  | <ol> <li>Identify the source.</li> <li>Notify IEC, ER, EPD and the Contractor within 24 hours of identification of the exceedance.</li> <li>Repeat measurement to confirm findings.</li> <li>Increase monitoring frequency.</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>Inform IEC, ER, and EPD the causes &amp; actions taken for the exceedances.</li> <li>Assess effectiveness of the Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> <li>If exceedance stops, cease additional monitoring</li> <li>Report the results of investigation to the IEC, EPD and ER.</li> </ol> | Discuss amongst ER, ET Leader and the Contractor on the potential remedial actions.     Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise ER accordingly.     Supervise the implementation of remedial measures. | Confirm receipt of notification of exceedance in writing.     Notify the Contractor.     Require the Contractor to propose remedial measures for the analysed noise problem.     Ensure remedial measures are properly implemented.     If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated. | 1. Take immediate action to avoid further exceedance. 2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification. 3. Implement the agreed proposals. 4. Resubmit proposals if problem still not under control. 5. Stop the relevant activity of works as determined by the ER until the exceedance is abated. |  |  |

## 3.4 Site Inspection and Environmental Complaint Handling

#### 3.4.1 Site Inspection

Site inspections provide a direct means to trigger and enforce the specified environmental protection and pollution control measures. They shall be undertaken routinely to inspect the construction activities to ensure appropriate environmental protection and pollution control/mitigation measures are properly implemented. With well-defined pollution control and mitigation specifications and a well-established site inspection, deficiency and action reporting system, site inspection is one of the most effective tools to enforce the environmental protection requirements on the construction site.

The ET Leader shall be responsible for formulating the environmental site inspection, deficiency and action reporting system, and carrying out the site inspection works. He shall

submit a proposal on site inspection, deficiency and action reporting procedures within 21 days prior to construction commencement to the Contractor for approval by the ER and IEC.

Regular site inspections shall be carried out at least once per week. The areas of inspection shall not be limited to the environmental conditions, pollution control and mitigation measures within the site. It should also review the environmental condition outside the site area which is likely to be affected, directly or indirectly, by the site activities. The ET Leader shall make reference to the following information in conducting the inspection:

- the EIA recommendations on environmental protection and pollution control mitigation measures:
- works progress and programme;
- individual works methodology (which shall include proposal on associated pollution control measures);
- Contract Specifications on environmental protection;
- relevant environmental protection and pollution control laws; and
- previous site inspection results.

The Contractor shall update ET Leader with all relevant information of the construction Contract for him to carry out the site inspections. The inspection results and its associated recommendations on improvements to the environmental protection and pollution control works shall be submitted to ER, IEC and the Contractor within 1 working day for reference and for taking immediate actions. The Contractor shall follow the procedures and time-frame as stipulated in the environmental site inspection, deficiency and action reporting system formulated by the ET Leader to report on any remedial measures subsequent to the site inspections.

Ad hoc site inspections shall also be carried out if significant environmental problems are identified. Inspections may also be required subsequent to receipt of an environmental complaint, or as part of the investigation work, as specified in the Action Plan for environmental monitoring and audit.

#### 3.4.2 Environmental Complaints

Complaints shall be referred to the ET Leader for carrying out complaint investigation. The ET Leader shall undertake the following procedures upon receipt of the complaints:

- log complaint and date of receipt onto the complaint database;
- investigate the complaint to determine its validity, and to assess whether the source of the problem is due to works activities;
- identify mitigation measures if a complaint is valid and due to works;
- advise the Contractor accordingly if mitigation measures are required;
- review the Contractor's response on the identified mitigation measures and the updated situation;
- submit interim report to ER on status of the complaint investigation and follow-up action within the time frame assigned by the ER;
- undertake additional monitoring and audit to verify the situation if necessary, and review that any valid reason for complaint does not recur;
- report the investigation results and the subsequent actions to the source of complaint for responding to complainant (If the source of complaint is EPD, the results should be reported within the time frame assigned by EPD); and
- record the complaint, investigation, the subsequent actions and the results in the monthly EM&A reports.

The Contractor and the ER shall also be notified of the nature of complaints. An investigation shall be initiated to determine the validity of the complaint and to identify the source of the problem. As necessary, the ER shall undertake the following steps:

- Investigate and identify the source of the problem;
- Liaise with the ET and IEC to identify remedial measures:
- Require the Contractor to take action to mitigate the situation;
- Repeat monitoring to check compliance with Action and Limit level; and
- Repeat review procedures to identify further possible areas of improvement if monitoring results show exceedances.

The outcome of the investigation and the action taken shall be documented on the complaints proforma. Where possible, a formal response to each complaint received shall be prepared, within a maximum of seven days, so as to notify the concerned person(s) that action has been taken.

All enquires which trigger this process shall be reported in the monthly EM&A reports which shall include results of inspections undertaken by site staff, and details of the measures taken, and additional monitoring results. It should be noted that the receipt of complaints or enquiries will not, in itself be sufficient reason to introduce additional mitigation measures. They will however initiate the Event/Action Plan and these procedures may lead to the introduction of mitigation measures if they are considered necessary. In all cases the complainant shall be notified of the findings of the Event/Action Plan and audit procedures put in place to ensure that the problem does not recur.

During the complaint investigation work, the Contractor and ER shall cooperate with the ET Leader in providing all the necessary information and assistance for completion of the investigation. If mitigation measures are identified in the investigation, the Contractor shall promptly carry out the mitigation. The ER shall ensure that the measures have been carried out by the Contractor.

The Contractor should provide a manned hotline (tape recording is not acceptable) to serve as the community liaison channel to complaints, comments, suggestions or requests for information during the construction and reinstatement of the Project, so that action can be immediately taken to reduce the environmental nuisance in response to complaints raised by nearby residents or relayed from other Government Department.

A flow chart of the complaint response procedures is shown in Figure 3-2 for reference.

#### 3.5 Environmental Mitigation Measures

Environmental mitigation measures as recommended in the EIA report were stipulated in the EM&A Manual for the Contractor to adopt. A list of mitigation measures and their implementation status are given in **Appendix C**.

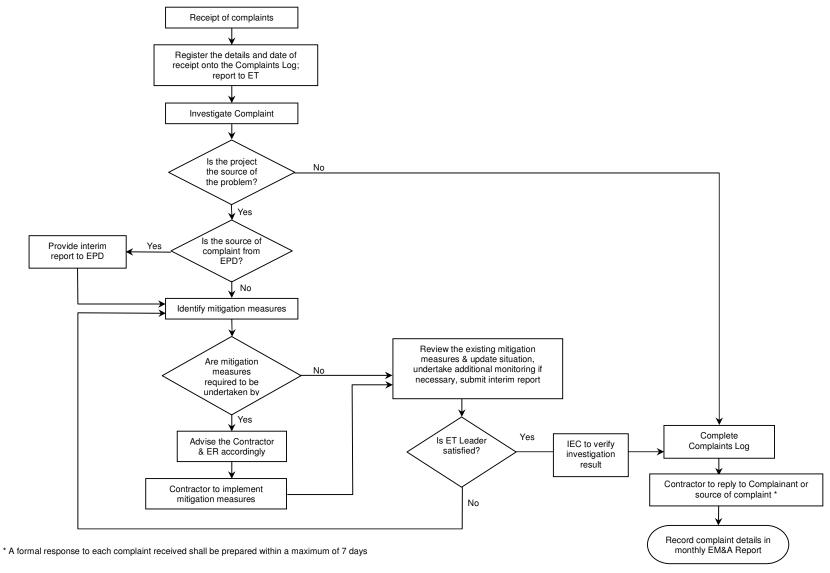


Figure 3-2: Flow chart of complaint response procedures

# 4 Noise Monitoring

#### 4.1 Monitoring Equipment

Details of the integrating sound level meters used in the noise monitoring are shown in Table 4-1.

Table 4-1: Equipment list for construction noise monitoring

| Equipment                     | Manufacturer & Model No. | Precision Grade | Qty. |
|-------------------------------|--------------------------|-----------------|------|
| Integrating sound level meter | Brüel & Kjær 2238        | IEC 651 Type 1  | 3    |
| Windshield                    | Brüel & Kjær UA0237      | IEC 804 Type 1  | 3    |
| Acoustical calibrator         | Brüel & Kjær 4231        | IEC 942 Type 1  | 1    |
| LCD wind speed indicator      | Kestrel Vane Anemometer  |                 | 1    |

#### 4.2 Methodology

#### 4.2.1 Field Measurement

- The sound level meter and battery were checked to ensure that they were in proper condition.
- The sound level meter was set on a tripod at 1.2m above ground and at 1m from the exterior of the building façade.
- Before conducting the measurement, the sound level meter was calibrated by an acoustical calibrator.
- The measurement parameter was set to A-weighted sound pressure level. The time weighting was set in fast response and the time period of measurement at 30 minutes.
- The wind speed was checked during noise monitoring to ensure the steady wind speed did not exceed 5m/s, or wind with gusts did not exceed 10m/s.
- Any abnormal conditions that generated intrusive noise during the measurement were recorded on the field record sheet.
- After each measurement, the equivalent continuous sound pressure level (Leq), L10 and L90 were recorded on the field record sheet.
- The sound level meter was re-calibrated by the acoustical calibrator to confirm that there was no significant drift of reading.

#### 4.2.2 Equipment Maintenance and Calibration

All sound level meters comply with the standards of IEC 651 (Fast, Slow, Impulse RMS detector tests) and IEC 804 ( $L_{eq}$  functions). The calibration certificates of the noise monitoring equipment are attached in **Appendix D**.

#### 4.3 Results and Observations

#### 4.3.1 Weather Conditions and Other Factors

No adverse weather conditions, in particular adverse wind speed & wind direction and fog & rain that may significantly affect or invalidate the collected noise monitoring data, were recorded during the reporting period.

Neither unusual operation of the construction site nor abnormal noise source was observed during the reporting period.

#### 4.3.2 Summary of Results

A total of 4 sets of daytime (0700 - 1900 hours) noise monitoring was conducted on 7, 13, 19 and 29 September 2007.

The highest noise level of 64.5 dB(A) was recorded at the roof of Racecourse Villa (NM2) on 7 September 2007 while the lowest noise level of 60.8 dB(A) was recorded at the podium outside Block 1 of Ravana Garden (NM3) on 13 September 2007. There was no exceedance of noise A/L Levels recorded during the reporting period.

Detailed construction noise monitoring results are attached in **Appendix E** and graphical presentation of the noise levels at each monitoring location is illustrated in Figure 4-1.

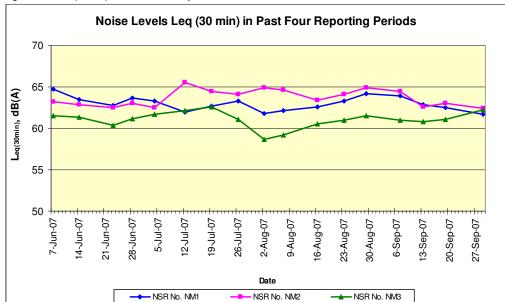


Figure 4-1: Graphical presentation of day-time noise levels

# 5 Landscape and Visual Monitoring and Audit

#### 5.1 Summary of Inspection

Landscape and visual monitoring and site audits were carried on 10 and 18 September 2007. Stables have been constructed. Planting Work has been completed. Transplanted trees and planted trees are generally in fair condition. The Contractor shall remove all wild climbers growing on transplanted trees and remove dead branches of retained trees. The audit findings and recommendations are recorded in a detailed report in **Appendix F**.

#### 5.2 Audit Schedule

Upcoming audits are scheduled for 5 and 22 October 2007.

# 6 Site Inspection, Waste Disposal, Environmental Complaints, Environmental Licenses and Non-compliance Records

#### 6.1 Site Audit Findings

Four weekly environmental site audits were carried out in September 2007. The findings of the site audits are summarised in Table 6-1.

Table 6-1: Findings of weekly environmental site audit in September 2007

| Date of Issue Raised | Observation   | Advice from EA | CT's Response /<br>Environmental<br>Outcomes | Closing Date |
|----------------------|---|----------------|--|--------------|
| 4 September<br>2007  | No construction works<br>during site audit. No<br>adverse environmental<br>impact was observed. | NIL            | N/A  | N/A          |
| 13 September<br>2007 | Restriction of access to stable area.     No adverse environmental impact was observed.         | NIL            | N/A  | N/A          |
| 17 September<br>2007 | No construction works<br>during site audit. No<br>adverse environmental<br>impact was observed. | NIL            | N/A  | N/A          |
| 24 September<br>2007 | 1. No construction works during site audit. No adverse environmental impact was observed.       | NIL            | N/A  | N/A          |

#### 6.2 Waste Disposal

Disposal of waste material during the reporting period generally complied with the corresponding waste disposal requirements. The waste disposal quantity during the reporting period is summarised in Table 6-2.

Table 6-2: Waste disposal quantity in September 2007

| Type of waste or<br>material  |  | Disposal at                     | No. of loads or quantities |
|-------------------------------|--|---------------------------------|----------------------------|
| C&D waste                     |  | SENT Landfill                   | 0 tonne                    |
| C&D material                  |  | Public Filling Area in TKO 137  | 0 tonne                    |
| Chemical Spent lube vaste oil |  | Collected by licensed collector | 0 L                        |

#### 6.3 Complaint Record

No environmental complaint was received during the reporting period.

A log record on the environmental complaints is given in **Appendix G** and a cumulative statistics on environmental complaints is given in Table 6-3.

**Table 6-3:** Cumulative statistics on environmental complaints

| No. of complaints received in the reporting month | No. of outstanding complaints | Cumulative no. of complaints received since the commencement of project |
|---|-------------------------------|---|
| 0   | 0                             | 22  |

#### 6.4 Exceedance

There was no exceedance of environmental monitoring data for A/L Levels during the reporting period.

#### 6.5 Notification of Summons and Successful Prosecution

No notification of summon and prosecution was received during the reporting month.

#### 6.6 Environmental Licenses

No new CNP was granted in the reporting period. A summary of the valid environmental licenses is given in Table 6-4.

Table 6-4: Summary of valid environmental licenses

| Type of Licence                    | Reference No.                 | Valid from    | Valid to         | Remarks                              |
|------------------------------------|-------------------------------|---------------|------------------|--------------------------------------|
| Environmental Permit               | EP-236/2006                   | 25 March 2006 |                  | -                                    |
| Construction Noise<br>Permit       | GW-RN0088-07                  | 6 March 2007  | 5 September 2007 | Cable laying                         |
| Construction Noise<br>Permit       | GW-RN0125-07                  | 6 April 2007  | 5 October 2007   | General earth and MS finishing works |
| Registration of Waste<br>Producer  | WPN:<br>5213-753-C331<br>7-11 | 1 Nov 2006    |                  | -                                    |
| Site Effluent<br>Discharge Licence | Licence No:<br>3448           | 1 Nov 2006    | 30 Nov 2011      | -                                    |

# 7 Future Key Issue

#### 7.1 Forecast of Works Programme

Pre-Test Event construction works was completed in mid July 2007. There will be no further construction works in the coming two months.

#### 7.2 Key Issues for Coming Month

The following key issue is anticipated in the coming month:

• Tree transplant and protection

# 8 Comments, Recommendations and Conclusion

#### 8.1 Comments and Recommendations

According to the environmental site inspections performed during the reporting period, the following recommendations were provided:

- Water Quality
  - Nil.
- Air Quality

- Nil.
- Construction Noise
  - Nil.
- Waste / Chemical Management
  - Nil.
- Landscape & Visual
  - Removal of all wild climbers on the transplanted trees areas; and
  - Removal all dead branches of retained trees.

#### 8.2 Conclusion

Construction phase impact monitoring and audit were conducted in the reporting month. Monitoring and audit programme included construction noise monitoring, landscape and visual monitoring and audit, and weekly site inspection.

Daytime noise levels were monitored at 3 monitoring locations during the reporting month. No exceedance of Limit Level was recorded.

Weekly site inspections were conducted in the reporting month. No adverse environmental impact was observed.

No new Construction Noise Permit was obtained in the reporting month.

No environmental complaint was received during the reporting period.

There was neither notification of summons nor prosecution received during the reporting period.

#### 9 References

- [1] Ove Arup & Partners Hong Kong Ltd. June 2006. Main Arena of the 2008 Olympic Equestrian Event Environmental Monitoring & Audit Manual
- [2] Ove Arup & Partners Hong Kong Ltd. July 2006. Main Arena of the 2008 Olympic Equestrian Event Environmental Baseline Monitoring Report

Appendix A
Construction Programme

(Construction Work has been Completed)

| ID | Task Name  | Duration | Early Start | Early Finish | uary February<br>1/8 /15 /22 /29 2/5 /12 /19 /26 | March April                             | May //23 //30 5/7 //14 | June          |
|----|--|----------|-------------|--------------|--|---|------------------------|---------------|
| 1  | Portion HKSI-1                                   | 57 days  | Jan 9 '07   | Mar 22 '07   | 1/0   13   22   23   2/3   12   19   20          | 3   3/3   12   19   20   4/2   4/9   10 | /23 /30  3/7 /14       | /21 //20  0/4 |
| 2  | Works in Veterinary Stable                       | 57 days  | Jan 9 '07   | Mar 22 '07   |  |   |                        |               |
| 3  | Building Envelope / External Finishes            | 25 days  | Jan 9 '07   | Feb 6 '07    |  |   |                        |               |
| 4  | Structural Steel Installation                    | 6 days   | Jan 17 '07  | Jan 23 '07   |  |   |                        |               |
| 5  | 1/F area structural steel installation           | 4 days   | Jan 17 '07  | Jan 20 '07   |  |   |                        |               |
| 6  | Office and General examination area              | 4 days   | Jan 19 '07  | Jan 23 '07   |  |   |                        |               |
| 7  | Roof Cladding and Gutter Installation            | 18 days  | Jan 17 '07  | Feb 6 '07    | , —  |   |                        |               |
| 8  | Plant Rooms area - upper roof                    | 2 days   | Jan 17 '07  | Jan 18 '07   |  |   |                        |               |
| 9  | Plant Rooms area - lower roof + gutter           | 6 days   | Jan 19 '07  | Jan 25 '07   |  |   |                        |               |
| 10 | Horse stalls area - upper roof                   | 6 days   | Jan 17 '07  | Jan 23 '07   |  |   |                        |               |
| 11 | Horse stalls area - lower roof                   | 12 days  | Jan 17 '07  | Jan 30 '07   |  |   |                        |               |
| 12 | 1/F AC Plant Room                                | 6 days   | Jan 31 '07  | Feb 6 '07    |  |   |                        |               |
| 13 | Granite Stone Installation                       | 8 days   | Jan 17 '07  | Jan 25 '07   | 1  |   |                        |               |
| 14 | 1/F Plant Rooms area external                    | 4 days   | Jan 17 '07  | Jan 20 '07   |  |   |                        |               |
| 15 | Tx room external                                 | 4 days   | Jan 22 '07  | Jan 25 '07   |  |   |                        |               |
| 16 | Stainless Steel Louver                           | 12 days  | Jan 17 '07  | Jan 30 '07   |  |   |                        |               |
| 17 | Plant Rooms area                                 | 6 days   | Jan 17 '07  | Jan 23 '07   |  |   |                        |               |
| 18 | Horse stalls area                                | 6 days   | Jan 24 '07  | Jan 30 '07   |  |   |                        |               |
| 19 | Precast Panel Installation                       | 10 days  | Jan 17 '07  | Jan 27 '07   |  |   |                        |               |
| 20 | Plant rooms areas                                | 4 days   | Jan 17 '07  | Jan 20 '07   |  |   |                        |               |
| 21 | Horse stalls area                                | 6 days   | Jan 17 '07  | Jan 23 '07   |  |   |                        |               |
| 22 | Office and general examination area              | 4 days   | Jan 24 '07  | Jan 27 '07   |  |   |                        |               |
| 23 | Metal Louvers                                    | 18 days  | Jan 9 '07   | Jan 29 '07   |  |   |                        |               |
| 24 | Remedial works at Tx Room                        | 12 days  | Jan 9 '07   | Jan 22 '07   |  |   |                        |               |
| 25 | Remedial works at Gen Set Room                   | 6 days   | Jan 23 '07  | Jan 29 '07   |  |   |                        |               |
| 26 | Internal ABWF and E&M Installation               | 56 days  | Jan 10 '07  | Mar 22 '07   |  |   |                        |               |
| 27 | Transformer Room                                 | 14 days  | Jan 16 '07  | Jan 31 '07   |  |   |                        |               |
| 28 | Wall tiles (RC Wall)                             | 2 days   | Jan 17 '07  | Jan 18 '07   |  |   |                        |               |
| 29 | Promat board to metal louver/metal door          | 2 days   | Jan 23 '07  | Jan 24 '07   |  |   |                        |               |
| 30 | E&M Access to COMEEL                             | 11 days  | Jan 16 '07  | Jan 27 '07   | 1/16   |   |                        |               |
| 31 | E&M Installation                                 | 10 days  | Jan 16 '07  | Jan 26 '07   |  |   |                        |               |
| 32 | E&M Final Fix + T&C                              | 4 days   | Jan 27 '07  | Jan 31 '07   |  |   |                        |               |
| 33 | Promat board blank off to stainless steel louver | 2 days   | Jan 24 '07  | Jan 25 '07   |  |   |                        |               |
| 34 | Structural steel bracing                         | 2 days   | Jan 22 '07  | Jan 23 '07   |  |   |                        |               |
| 35 | Promat board ceiling installation                | 2 days   | Jan 24 '07  | Jan 25 '07   |  |   |                        |               |
| 36 | Painting works (ceiling)                         | 2 days   | Jan 26 '07  | Jan 27 '07   |  |   |                        |               |
| 37 | Epoxy floor painting                             | 2 days   | Jan 29 '07  | Jan 30 '07   |  |   |                        |               |
| 38 | Cable trench cover installation                  | 1 day    | Jan 31 '07  | Jan 31 '07   |  |   |                        |               |
|    |  | Task     |             |              | Milestone •                                      | External Tas                            | sks                    |               |
|    | onths Rolling Programme_MP06                     | Split    |             |              | Summary  | External Mile                           | estone 🌰               |               |
|    | Prepared: Jan 23 '07                             | Progres  |             |              | Project Summary                                  | Deadline                                |                        |               |


| ID   | Task Name   | Duration | Early Start | Early Finish | Uary   February   March   April   May   June   1/8   /15   /22   /29   2/5   /12   /19   /26   3/5   /12   /19   /26   4/2   4/9   /16   /23   /30   5/7   /14   /21   /28   6/4   / |
|------|---|----------|-------------|--------------|--|
| 39   | CLP Installation at Transformer Room              | 56 days  | Jan 10 '07  | Mar 22 '07   |  |
| 40   | Pre inspection                                    | 1 day    | Jan 10 '07  | Jan 10 '07   | 1/10   |
| 41   | Handover Inspection                               | 1 day    | Feb 1 '07   | Feb 1 '07    | ■ <b>▼</b>   |
| 42   | CLP Installation                                  | 36 days  | Feb 1 '07   | Mar 21 '07   |  |
| 43   | Power On  | 1 day    | Mar 22 '07  | Mar 22 '07   | 3/22   |
| 44   | New Switch Room/FS Tank/ Fuel Tank room           | 18 days  | Jan 23 '07  | Feb 19 '07   |  |
| 45   | Wall tiles (RC Wall)                              | 2 days   | Jan 23 '07  | Jan 24 '07   |  |
| 46   | Promat board to metal louver/metal door           | 2 days   | Jan 30 '07  | Jan 31 '07   |  |
| 47   | Painting to wall                                  | 1 day    | Feb 1 '07   | Feb 1 '07    |  |
| 48   | E&M Access to COMEEL                              | 1 day    | Jan 26 '07  | Jan 26 '07   | 1/26   |
| 49   | E&M Installation                                  | 11 days  | Jan 26 '07  | Feb 7 '07    |  |
| 50   | E&M Final Fix + T&C                               | 4 days   | Feb 8 '07   | Feb 19 '07   |  |
| 51   | Promat board blank off to stainless steel louver  | 2 days   | Jan 24 '07  | Jan 25 '07   |  |
| 52   | Structural steel bracing at roof                  | 2 days   | Jan 24 '07  | Jan 25 '07   |  |
| 53   | Promat board ceiling installation                 | 2 days   | Jan 26 '07  | Jan 27 '07   |  |
| 54   | Painting works (ceiling)                          | 2 days   | Jan 29 '07  | Jan 30 '07   |  |
| 55   | Epoxy floor painting                              | 2 days   | Jan 31 '07  | Feb 1 '07    |  |
| 56   | Cable trench cover installation                   | 1 day    | Feb 2 '07   | Feb 2 '07    |  |
| 57   | Feed Tack, Wash Bay, Changing Rm, Lavatory Areas  | 12 days  | Jan 17 '07  | Jan 30 '07   |  |
| 58   | Internal block works                              | 10 days  | Jan 17 '07  | Jan 27 '07   |  |
| 59   | Plastering  | 10 days  | Jan 19 '07  | Jan 30 '07   |  |
| 60   | 1/F AC Plant Room                                 | 8 days   | Jan 22 '07  | Jan 30 '07   |  |
| 61   | Structural steel installation complete            | 1 day    | Jan 22 '07  | Jan 22 '07   | 1/22   |
| 62   | RC Wall and slab                                  | 6 days   | Jan 23 '07  | Jan 29 '07   |  |
| 63   | AHU installation                                  | 1 day    | Jan 30 '07  | Jan 30 '07   | 1/30   |
| 64   | Works in Main Stable No.1                         | 33 days  | Jan 17 '07  | Mar 2 '07    |  |
| 65   | RC Works  | 8 days   | Jan 30 '07  | Feb 7 '07    |  |
| 66   | Sand rolls wall construction                      | 8 days   | Jan 30 '07  | Feb 7 '07    |  |
| 67   | Building Envelope / External Finishes             | 33 days  | Jan 17 '07  | Mar 2 '07    |  |
| 68   | Structural Steel Installation                     | 7 days   | Jan 17 '07  | Jan 24 '07   |  |
| 69   | Wing 1 - 1/F AC Plant Room                        | 5 days   | Jan 17 '07  | Jan 22 '07   |  |
| 70   | Wing 2 - 1/F AC Plant Room                        | 7 days   | Jan 17 '07  | Jan 24 '07   |  |
| 71   | Center Wing (Office area)                         | 6 days   | Jan 17 '07  | Jan 23 '07   |  |
| 72   | Roof Cladding and Gutter Installation             | 19 days  | Jan 17 '07  | Feb 7 '07    |  |
| 73   | Wing 1 (Horse Stalls) and 1/F Plant Rooms         | 17 days  | Jan 17 '07  | Feb 5 '07    |  |
| 74   | Horse stall area - upper roof                     | 9 days   | Jan 17 '07  | Jan 26 '07   |  |
| 75   | Horse stall area - lower roof                     | 9 days   | Jan 17 '07  | Jan 26 '07   |  |
| 76   | 1/F AC Plant Room                                 | 4 days   | Feb 1 '07   | Feb 5 '07    |  |
|      | <u> </u>  | 1        |             |              |  |
| ) NA | onthe Polling Programme MD06                      | Task     |             |              | Milestone External Tasks   |
|      | onths Rolling Programme_MP06 Prepared: Jan 23 '07 | Split    |             |              | Summary External Milestone   |
| Jale | riepaieu. Jaii 23 VI                              | Progres  | ss          |              | Project Summary Deadline   |

| ID   | Task Name                                     | Duration | Early Start | Early Finish | Uary   February   March   April   May   June   1/8  /15  /22  /29  2/5  /12  /19  /26  3/5  /12  /19  /26  4/2  4/9  /16  /23  /30  5/7  /14  /21  /28  6/4  /1 |
|------|---|----------|-------------|--------------|---|
| 77   | Wing 2 (Horse Stalls) and 1/F Plant Rooms     | 10 days  | Jan 27 '07  | Feb 7 '07    |   |
| 78   | Horse stall area - upper roof                 | 6 days   | Jan 27 '07  | Feb 2 '07    | 7   |
| 79   | Horse stall area - lower roof                 | 6 days   | Jan 31 '07  | Feb 6 '07    |   |
| 80   | 1/F AC Plant Room                             | 4 days   | Feb 3 '07   | Feb 7 '07    | 7   |
| 81   | Center Wing (Office Area)                     | 6 days   | Jan 24 '07  | Jan 30 '07   | 7   |
| 82   | Horse stall area - upper roof                 | 4 days   | Jan 24 '07  | Jan 27 '07   | 7   |
| 83   | Horse stall area - lower roof                 | 4 days   | Jan 26 '07  | Jan 30 '07   | 7   |
| 84   | Granite Stone Installation                    | 33 days  | Jan 17 '07  | Mar 2 '07    |   |
| 85   | Wing 1 - Grid 1-4 Corner                      | 12 days  | Jan 17 '07  | Jan 30 '07   | 7   |
| 86   | Wing 2 - Grid 13-16 Corner                    | 12 days  | Jan 17 '07  | Jan 30 '07   |   |
| 87   | Wing 1 - Horse stall areas                    | 12 days  | Jan 27 '07  | Feb 9 '07    |   |
| 88   | Wing 2 - Horse stall areas                    | 12 days  | Feb 3 '07   | Feb 23 '07   |   |
| 89   | Office areas                                  | 12 days  | Feb 10 '07  | Mar 2 '07    |   |
| 90   | Precast Panel Installation                    | 21 days  | Jan 17 '07  | Feb 9 '07    | 7   |
| 91   | Wing 1 - Horse stall areas                    | 9 days   | Jan 17 '07  | Jan 26 '07   |   |
| 92   | Wing 2 - Horse stall areas                    | 6 days   | Jan 27 '07  | Feb 2 '07    | 7   |
| 93   | Office areas                                  | 6 days   | Feb 3 '07   | Feb 9 '07    | 7   |
| 94   | Internal ABWF and E&M Installation            | 15 days  | Jan 17 '07  | Feb 2 '07    | 7   |
| 95   | Wing 1 (Horse Stall) Grid 1-4                 | 9 days   | Jan 17 '07  | Jan 26 '07   | 7   |
| 96   | Horse stall - internal partions/blockworks    | 6 days   | Jan 17 '07  | Jan 23 '07   |   |
| 97   | Wall Plastering                               | 3 days   | Jan 24 '07  | Jan 26 '07   |   |
| 98   | Roller shutter installation                   | 3 days   | Jan 20 '07  | Jan 23 '07   | 7   |
| 99   | Wing 2 (Horse Stall), Grid 13-16              | 12 days  | Jan 17 '07  | Jan 30 '07   |   |
| 100  | Horse stall - internal partitions/block works | 6 days   | Jan 17 '07  | Jan 23 '07   |   |
| 101  | Wall plastering                               | 3 days   | Jan 24 '07  | Jan 26 '07   | 7   |
| 102  | Roller shutter installation                   | 3 days   | Jan 27 '07  | Jan 30 '07   | 7   |
| 103  | 1/F AC Plant Room, Grid 1-4                   | 8 days   | Jan 23 '07  | Jan 31 '07   | 7   |
| 104  | Structural steel installation complete        | 1 day    | Jan 23 '07  | Jan 23 '07   | 7 1/23  |
| 105  | RC Wall and slab                              | 6 days   | Jan 24 '07  | Jan 30 '07   | 7   |
| 106  | AHU installation                              | 1 day    | Jan 31 '07  | Jan 31 '07   | 7   |
| 107  | 1/F AC Plant Room, Grid 13-16                 | 8 days   | Jan 25 '07  | Feb 2 '07    | 7   |
| 108  | Structural steel installation complete        | 1 day    | Jan 25 '07  | Jan 25 '07   | 7 1/25  |
| 109  | RC Wall and slab                              | 6 days   | Jan 26 '07  | Feb 1 '07    | 7   |
| 110  | AHU installation                              | 1 day    | Feb 2 '07   | Feb 2 '07    | 7   |
| 111  | Center Wing - Office Areas                    | 15 days  | Jan 17 '07  | Feb 2 '07    | 7   |
| 112  | Internal partions/blockworks                  | 12 days  | Jan 17 '07  | Jan 30 '07   |   |
| 113  | Wall Plastering                               | 3 days   | Jan 31 '07  | Feb 2 '07    |   |
| 114  | Works in Main Stable No.2                     | 26 days  | Jan 17 '07  | Feb 22 '07   | 7   |
|      |   | Task     |             |              | Milestone   |
| 3 Mc | onths Rolling Programme_MP06                  | Split    |             |              | Summary External Milestone  |
|      | Prepared: Jan 23 '07                          | -        |             |              |   |
|      | •   | Progre   | ss          |              | Project Summary Deadline  |

| ID          | Task Name   | Duration | Early Start       | Early Finish | uary   February   March   April   May   June   1/8  /15  /22  /29  2/5  /12  /19  /26  3/5  /12  /19  /26  4/2  4/9  /16  /23  /30  5/7  /14  /21  /28  6/4  /2 |
|-------------|---|----------|-------------------|--------------|---|
| 115         | RC Works  | 6 days   | Jan 26 '07        | Feb 1 '07    |   |
| 116         | Sand rolls wall construction                      | 6 days   | Jan 26 '07        | Feb 1 '07    | 7   |
| 117         | Building Envelope / External Finishes             | 26 days  | Jan 17 '07        | Feb 22 '07   | 7   |
| 118         | Structural Steel Installation                     | 12 days  | Jan 17 '07        | Jan 30 '07   | 7   |
| 119         | Wing 1 - Horse stall areas                        | 9 days   | Jan 17 '07        | Jan 26 '07   | 7   |
| 120         | Wing 2 - Horse stalls areas                       | 9 days   | Jan 17 '07        | Jan 26 '07   | 7   |
| 121         | Wing 1 - 1/F AC Plant Room                        | 9 days   | Jan 20 '07        | Jan 30 '07   | 7   |
| 122         | Wing 2 - 1/F AC Plant Room                        | 9 days   | Jan 20 '07        | Jan 30 '07   | 7   |
| 123         | Center Wing (Office area)                         | 5 days   | Jan 23 '07        | Jan 27 '07   | 7   |
| 124         | Roof Cladding and Gutter Installation             | 21 days  | Jan 20 '07        | Feb 20 '07   | 7   |
| 125         | Wing 1 (Horse Stalls) and 1/F Plant Rooms         | 21 days  | Jan 20 '07        | Feb 20 '07   | 7   |
| 126         | Horse stall area - upper roof                     | 4 days   | Jan 27 '07        | Jan 31 '07   | 7   |
| 127         | Horse stall area - lower roof                     | 10 days  | Jan 20 '07        | Jan 31 '07   | 7   |
| 128         | 1/F AC Plant Room                                 | 4 days   | Feb 9 '07         | Feb 20 '07   | 7   |
| 129         | Wing 2 (Horse Stalls) and 1/F Plant Rooms         | 21 days  | Jan 20 '07        | Feb 20 '07   | 7   |
| 130         | Horse stall area - upper roof                     | 4 days   | Jan 27 '07        | Jan 31 '07   | 7   |
| 131         | Horse stall area - lower roof                     | 10 days  | Jan 20 '07        | Jan 31 '07   | 7   |
| 132         | 1/F AC Plant Room                                 | 4 days   | Feb 9 '07         | Feb 20 '07   | 7   |
| 133         | Center Wing (Office Area)                         | 8 days   | Jan 29 '07        | Feb 6 '07    | 7   |
| 134         | Horse stall area - upper roof                     | 4 days   | Jan 29 '07        | Feb 1 '07    | 7   |
| 135         | Horse stall area - lower roof                     | 4 days   | Feb 2 '07         | Feb 6 '07    | 7   |
| 136         | Granite Stone Installation                        | 26 days  | Jan 17 '07        | Feb 22 '07   | 7   |
| 137         | Wing 1 - Grid 1-4 Corner                          | 12 days  | Jan 17 '07        | Jan 30 '07   | 7   |
| 138         | Wing 2 - Grid 13-16 Corner                        | 12 days  | Jan 17 '07        | Jan 30 '07   | 7   |
| 139         | Wing 1 - Horse stall areas                        | 12 days  | Jan 24 '07        | Feb 6 '07    | 7   |
| 140         | Wing 2 - Horse stall areas                        | 12 days  | Jan 26 '07        | Feb 8 '07    | 7   |
| 141         | Office areas                                      | 12 days  | Feb 2 '07         | Feb 22 '07   | 7   |
| 142         | Precast Panel Installation                        | 14 days  | Jan 17 '07        | Feb 1 '07    | 7   |
| 143         | Wing 1 - Horse stall areas                        | 6 days   | Jan 17 '07        | Jan 23 '07   | 7   |
| 144         | Wing 2 - Horse stall areas                        | 6 days   | Jan 19 '07        | Jan 25 '07   | 7   |
| 145         | Office areas                                      | 6 days   | Jan 26 '07        | Feb 1 '07    | 7   |
| 146         | Internal ABWF and E&M Installation                | 23 days  | Jan 17 '07        | Feb 19 '07   | 7   |
| 147         | Wing 1 (Horse Stall) Grid 1-4                     | 12 days  | Jan 17 '07        | Jan 30 '07   | 7   |
| 148         | Horse stall - internal partions/blockworks        | 6 days   | Jan 17 '07        | Jan 23 '07   | 7   |
| 149         | Wall Plastering                                   | 3 days   | Jan 24 '07        | Jan 26 '07   | 7   |
| 150         | Roller shutter installation                       | 3 days   | Jan 27 '07        | Jan 30 '07   |   |
| 151         | Wing 2 (Horse Stall), Grid 13-16                  | 12 days  | Jan 17 '07        | Jan 30 '07   |   |
| 152         | Horse stall - internal partitions/block works     | 6 days   | Jan 17 '07        | Jan 23 '07   | 7   |
|             |   |          | l l               |              |   |
| <b>В</b> ВЛ | onthe Polling Programme MD06                      | Task     |                   |              | Milestone External Tasks  |
|             | onths Rolling Programme_MP06 Prepared: Jan 23 '07 | Split    | 111               |              | Summary External Milestone  |
| Jale        | riepaieu. Jaii 23 u <i>i</i>                      | Progre   | ss $\blacksquare$ |              | Project Summary Deadline  |

| ID    | Task Name   | Duration | Early Start | Early Finish | uary February March   | April   May   June   26  4/2  4/9  /16  /23  /30  5/7  /14  /21  /28  6/4  /11 |
|-------|---|----------|-------------|--------------|---|--|
| 153   | Wall plastering                                       | 3 days   | Jan 24 '07  | Jan 26 '07   | 110 / 13 / 22 / 23 / 213 / 12 / 13 / 20   5/3 / 12 / 19 / 2 | 20 11/2 11/3 y 10 y 20 y 00 p/1 y 14 y 21 y 20 p/14 y 11                       |
| 154   | Roller shutter installation                           | 3 days   | Jan 27 '07  | Jan 30 '07   |   |  |
| 155   | 1/F AC Plant Room, Grid 1-4                           | 8 days   | Jan 31 '07  | Feb 8 '07    |   |  |
| 156   | Structural steel installation complete                | 1 day    | Jan 31 '07  | Jan 31 '07   | 1/31  |  |
| 157   | RC Wall and slab                                      | 6 days   | Feb 1 '07   | Feb 7 '07    |   |  |
| 158   | AHU installation                                      | 1 day    | Feb 8 '07   | Feb 8 '07    |   |  |
| 159   | 1/F AC Plant Room, Grid 13-16                         | 8 days   | Jan 31 '07  | Feb 8 '07    |   |  |
| 160   | Structural steel installation complete                | 1 day    | Jan 31 '07  | Jan 31 '07   | 1/31  |  |
| 161   | RC Wall and slab                                      | 6 days   | Feb 1 '07   | Feb 7 '07    |   |  |
| 162   | AHU installation                                      | 1 day    | Feb 8 '07   | Feb 8 '07    |   |  |
| 163   | Center Wing - Office Areas                            | 9 days   | Feb 2 '07   | Feb 19 '07   |   |  |
| 164   | Internal partions/blockworks                          | 6 days   | Feb 2 '07   | Feb 8 '07    |   |  |
| 165   | Wall Plastering                                       | 3 days   | Feb 9 '07   | Feb 19 '07   |   |  |
| 166   | Works in Main Stable No.3                             | 32 days  | Jan 17 '07  | Mar 1 '07    |   |  |
| 167   | RC Works  | 12 days  | Jan 17 '07  | Jan 30 '07   |   |  |
| 168   | Remaining grade slab and sand rolls slab construction | 6 days   | Jan 17 '07  | Jan 23 '07   |   |  |
| 169   | Sand rolls wall construction                          | 6 days   | Jan 24 '07  | Jan 30 '07   |   |  |
| 170   | Building Envelope / External Finishes                 | 32 days  | Jan 17 '07  | Mar 1 '07    |   |  |
| 171   | Structural Steel Installation                         | 10 days  | Jan 23 '07  | Feb 2 '07    |   |  |
| 172   | Wing 1 - Horse stall areas                            | 6 days   | Jan 23 '07  | Jan 29 '07   |   |  |
| 173   | Wing 2 - Horse stalls areas                           | 6 days   | Jan 23 '07  | Jan 29 '07   | -   |  |
| 174   | Wing 1 - 1/F AC Plant Room                            | 4 days   | Jan 30 '07  | Feb 2 '07    |   |  |
| 175   | Wing 2 - 1/F AC Plant Room                            | 4 days   | Jan 30 '07  | Feb 2 '07    |   |  |
| 176   | Center Wing (Office area)                             | 4 days   | Jan 30 '07  | Feb 2 '07    |   |  |
| 177   | Roof Cladding and Gutter Installation                 | 20 days  | Jan 30 '07  | Feb 28 '07   |   |  |
| 178   | Wing 1 (Horse Stalls) and 1/F Plant Rooms             | 16 days  | Jan 30 '07  | Feb 23 '07   |   |  |
| 179   | Horse stall area - upper roof                         | 4 days   | Jan 30 '07  | Feb 2 '07    |   |  |
| 180   | Horse stall area - lower roof                         | 6 days   | Feb 3 '07   | Feb 9 '07    |   |  |
| 181   | 1/F AC Plant Room                                     | 4 days   | Feb 20 '07  | Feb 23 '07   |   |  |
| 182   | Wing 2 (Horse Stalls) and 1/F Plant Rooms             | 16 days  | Jan 30 '07  | Feb 23 '07   |   |  |
| 183   | Horse stall area - upper roof                         | 4 days   | Jan 30 '07  | Feb 2 '07    | 1   |  |
| 184   | Horse stall area - lower roof                         | 6 days   | Feb 3 '07   | Feb 9 '07    |   |  |
| 185   | 1/F AC Plant Room                                     | 4 days   | Feb 20 '07  | Feb 23 '07   |   |  |
| 186   | Center Wing (Office Area)                             | 16 days  | Feb 3 '07   | Feb 28 '07   |   |  |
| 187   | Horse stall area - upper roof                         | 4 days   | Feb 3 '07   | Feb 7 '07    |   |  |
| 188   | Horse stall area - lower roof                         | 12 days  | Feb 8 '07   | Feb 28 '07   | <u> </u>  |  |
| 189   | Granite Stone Installation                            | 32 days  | Jan 17 '07  | Mar 1 '07    |   |  |
| 190   | Wing 1 - Grid 1-4 Corner                              | 12 days  |             | Jan 30 '07   |   |  |
|       |   |          |             |              |   |  |
| R Ma  | onths Rolling Programme_MP06                          | Task     |             |              | Milestone   | External Tasks   |
|       | Prepared: Jan 23 '07                                  | Split    | 111         |              | Summary   | External Milestone   |
| ait I | Tepared. Jan 25 VI                                    | Progres  | ss          |              | Project Summary   | Deadline   |

| ID  | Task Name   | Duration | Early Start | Early Finish | uary February March April May June  |
|-----|---|----------|-------------|--------------|---|
| 191 | Wing 2 - Grid 13-16 Corner                            | 12 days  | Jan 17 '07  | Jan 30 '07   | 1/8  /15  /22  /29  2/5  /12  /19  /26  3/5  /12  /19  /26  4/2  4/9  /16  /23  /30  5/7  /14  /21  /28  6/4  /11 |
| 192 | Wing 1 - Horse stall areas                            | 12 days  | Jan 31 '07  | Feb 20 '07   |   |
| 193 | Wing 2 - Horse stall areas                            | 12 days  | Feb 2 '07   | Feb 22 '07   | 7   |
| 194 | Office areas  | 12 days  | Feb 9 '07   | Mar 1 '07    |   |
| 195 | Precast Panel Installation                            | 20 days  | Jan 17 '07  | Feb 8 '07    |   |
| 196 | Wing 1 - Horse stall areas                            | 12 days  | Jan 17 '07  | Jan 30 '07   |   |
| 197 | Wing 2 - Horse stall areas                            | 8 days   | Jan 24 '07  | Feb 1 '07    |   |
| 198 | Office areas  | 6 days   | Feb 2 '07   | Feb 8 '07    |   |
| 199 | Internal ABWF and E&M Installation                    | 28 days  |             | Feb 24 '07   |   |
| 200 | Wing 1 (Horse Stall) Grid 1-4                         | 18 days  |             | Feb 6 '07    |   |
| 201 | Horse stall - internal partions/blockworks            | 12 days  | Jan 17 '07  | Jan 30 '07   |   |
| 202 | Wall Plastering                                       | 3 days   | Jan 31 '07  | Feb 2 '07    |   |
| 203 | Roller shutter installation                           | 3 days   | Feb 3 '07   | Feb 6 '07    |   |
| 204 | Wing 2 (Horse Stall), Grid 13-16                      | 18 days  | Jan 17 '07  | Feb 6 '07    |   |
| 205 | Horse stall - internal partitions/block works         | 12 days  | Jan 17 '07  | Jan 30 '07   |   |
| 206 | Wall plastering                                       | 3 days   | Jan 31 '07  | Feb 2 '07    |   |
| 207 | Roller shutter installation                           | 3 days   | Feb 3 '07   | Feb 6 '07    |   |
| 208 | 1/F AC Plant Room, Grid 1-4                           | 8 days   | Feb 3 '07   | Feb 19 '07   |   |
| 209 | Structural steel installation complete                | 1 day    | Feb 3 '07   | Feb 3 '07    | 2/3   |
| 210 | RC Wall and slab                                      | 6 days   | Feb 5 '07   | Feb 10 '07   | 7   |
| 211 | AHU installation                                      | 1 day    | Feb 19 '07  | Feb 19 '07   | 7   |
| 212 | 1/F AC Plant Room, Grid 13-16                         | 8 days   | Feb 3 '07   | Feb 19 '07   |   |
| 213 | Structural steel installation complete                | 1 day    | Feb 3 '07   | Feb 3 '07    | 7 2/3   |
| 214 | RC Wall and slab                                      | 6 days   | Feb 5 '07   | Feb 10 '07   |   |
| 215 | AHU installation                                      | 1 day    | Feb 19 '07  | Feb 19 '07   | 7   |
| 216 | Center Wing - Office Areas                            | 9 days   | Feb 8 '07   | Feb 24 '07   |   |
| 217 | Internal partions/blockworks                          | 6 days   | Feb 8 '07   | Feb 21 '07   | 7   |
| 218 | Wall Plastering                                       | 3 days   | Feb 22 '07  | Feb 24 '07   |   |
| 219 | Works in Main Stable No.4                             | 46 days  | Jan 17 '07  | Mar 17 '07   |   |
| 220 | RC Works  | 12 days  | Jan 17 '07  | Jan 30 '07   |   |
| 221 | Internal RC Wall partition                            | 6 days   | Jan 17 '07  | Jan 23 '07   |   |
| 222 | Remaining grade slab and sand rolls slab construction | 6 days   | Jan 17 '07  | Jan 23 '07   |   |
| 223 | Sand rolls wall construction                          | 6 days   | Jan 24 '07  | Jan 30 '07   |   |
| 224 | Building Envelope / External Finishes                 | 46 days  | Jan 17 '07  | Mar 17 '07   |   |
| 225 | Structural Steel Installation                         | 10 days  | Jan 30 '07  | Feb 9 '07    |   |
| 226 | Wing 1 - Horse stall areas                            | 6 days   | Jan 30 '07  | Feb 5 '07    |   |
| 227 | Wing 2 - Horse stalls areas                           | 6 days   | Jan 30 '07  | Feb 5 '07    |   |
| 228 | Wing 1 - 1/F AC Plant Room                            | 4 days   | Feb 6 '07   | Feb 9 '07    |   |
|     |   | Task     |             |              | Milestone   |
| 3 M | onths Rolling Programme_MP06                          |          |             |              |   |
|     | Prepared: Jan 23 '07                                  | Split    |             |              |   |
|     | •   | Progre   | SS          |              | Project Summary Deadline  |

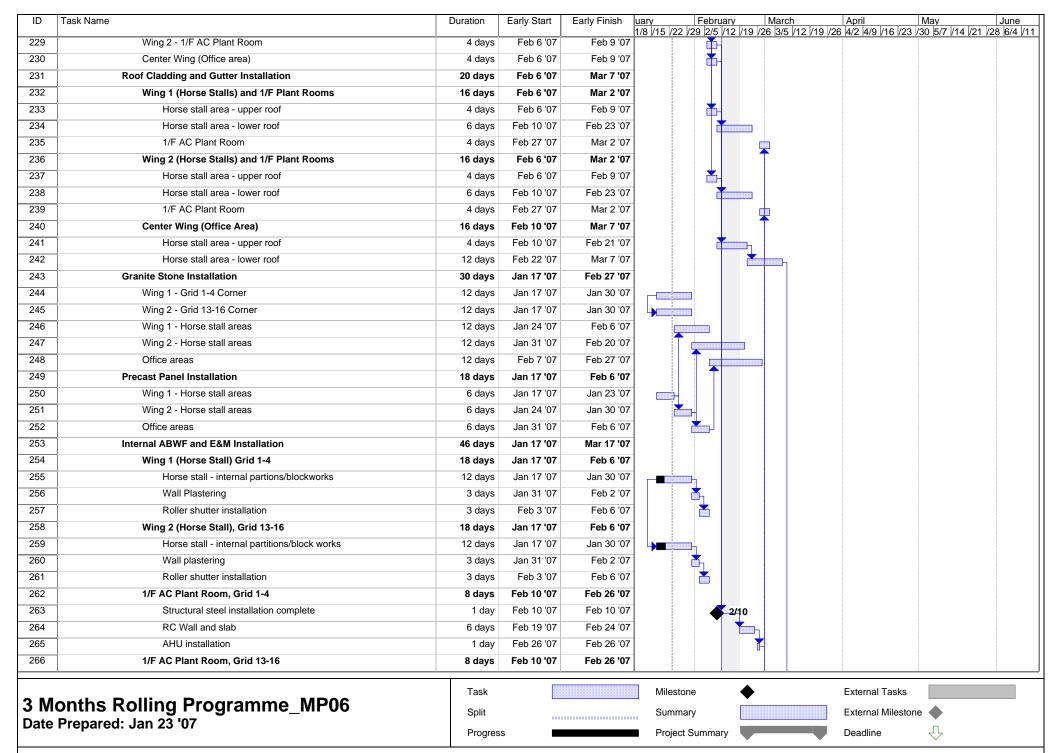


| ID   | Task Name                              | Duration | Early Start | Early Finish | Uary   February   March   April   May   June   1/8  /15  /22  /29  2/5  /12  /19  /26  3/5  /12  /19  /26  4/2  4/9  /16  /23  /30  5/7  /14  /21  /28  6/4 |
|------|--|----------|-------------|--------------|---|
| 267  | Structural steel installation complete | 1 day    | Feb 10 '07  | Feb 10 '07   | 7 2/10  |
| 268  | RC Wall and slab                       | 6 days   | Feb 19 '07  | Feb 24 '07   |   |
| 269  | AHU installation                       | 1 day    | Feb 26 '07  | Feb 26 '07   | 7   |
| 270  | Center Wing - Office Areas             | 9 days   | Mar 8 '07   | Mar 17 '07   | 7   |
| 271  | Internal partions/blockworks           | 6 days   | Mar 8 '07   | Mar 14 '07   | 7   |
| 272  | Wall Plastering                        | 3 days   | Mar 15 '07  | Mar 17 '07   |   |
| 273  | External Drainage Works                | 20 days  | Jan 17 '07  | Feb 8 '07    |   |
| 274  | Drainage MHS13.6 to MHS13.7, DN450     | 4 days   | Jan 17 '07  | Jan 20 '07   | 7   |
| 275  | Excavation                             | 1 day    | Jan 17 '07  | Jan 17 '07   | 7 <b>B</b> 7  |
| 276  | Pipelaying                             | 1 day    | Jan 18 '07  | Jan 18 '07   |   |
| 277  | Manhole construction                   | 1 day    | Jan 19 '07  | Jan 19 '07   |   |
| 278  | Backfilling                            | 1 day    | Jan 20 '07  | Jan 20 '07   |   |
| 279  | Drainage MHS13.7 to MHS13.7A, DN225    | 4 days   | Jan 23 '07  | Jan 26 '07   |   |
| 280  | Excavation                             | 1 day    | Jan 23 '07  | Jan 23 '07   |   |
| 281  | Pipelaying                             | 1 day    | Jan 24 '07  | Jan 24 '07   |   |
| 282  | Manhole construction                   | 1 day    | Jan 25 '07  | Jan 25 '07   |   |
| 283  | Backfilling                            | 1 day    | Jan 26 '07  | Jan 26 '07   |   |
| 284  | Drainage MHS13.7A to MHS13.8, DN225    | 4 days   | Jan 24 '07  | Jan 27 '07   |   |
| 285  | Excavation                             | 1 day    | Jan 24 '07  | Jan 24 '07   |   |
| 286  | Pipelaying                             | 1 day    | Jan 25 '07  | Jan 25 '07   |   |
| 287  | Manhole construction                   | 1 day    | Jan 26 '07  | Jan 26 '07   |   |
| 288  | Backfilling                            | 1 day    | Jan 27 '07  | Jan 27 '07   |   |
| 289  | Drainage MHS13.8 to MHS13.9, DN225     | 4 days   | Jan 25 '07  | Jan 29 '07   |   |
| 290  | Excavation                             | 1 day    | Jan 25 '07  | Jan 25 '07   |   |
| 291  | Pipelaying                             | 1 day    | Jan 26 '07  | Jan 26 '07   |   |
| 292  | Manhole construction                   | 1 day    | Jan 27 '07  | Jan 27 '07   |   |
| 293  | Backfilling                            | 1 day    | Jan 29 '07  | Jan 29 '07   |   |
| 294  | Drainage MHSVS40 to MHSVS38, DN300     | 7 days   | Jan 17 '07  | Jan 24 '07   |   |
| 295  | Excavation                             | 2 days   | Jan 17 '07  | Jan 18 '07   | 7 📭   |
| 296  | Pipelaying                             | 2 days   | Jan 19 '07  | Jan 20 '07   |   |
| 297  | Manhole construction                   | 2 days   | Jan 22 '07  | Jan 23 '07   |   |
| 298  | Backfilling                            | 1 day    | Jan 24 '07  | Jan 24 '07   |   |
| 299  | Drainage MHS13.11 to MHS13.12, DN225   | 6 days   | Jan 17 '07  | Jan 23 '07   |   |
| 300  | Excavation                             | 1 day    | Jan 17 '07  | Jan 17 '07   | 7 h   |
| 301  | Pipelaying                             | 2 days   | Jan 18 '07  | Jan 19 '07   |   |
| 302  | Manhole construction                   | 2 days   | Jan 20 '07  | Jan 22 '07   |   |
| 303  | Backfilling                            | 1 day    | Jan 23 '07  | Jan 23 '07   |   |
| 304  | Drainage MHS13.11 to MHS13.10, DN225   | 7 days   | Jan 24 '07  | Jan 31 '07   |   |
|      |  | Task     |             |              | Milestone   |
|      | onths Rolling Programme_MP06           | Split    | 111         |              | Summary External Milestone  |
| Jate | Prepared: Jan 23 '07                   | Progre   |             |              | ■ Project Summary Deadline  |


| ID   | Task Name  | Duration | Early Start | Early Finish | Leary   February   March   April   May   Jun   1/8   1/5   1/22   1/29   2/5   1/12   1/19   2/26   3/5   1/12   1/19   2/26   4/2   4/9   1/16   1/23   3/30   5/7   1/14   1/21   1/28   6/4   1/2 |
|------|--|----------|-------------|--------------|--|
| 305  | Excavation   | 2 days   | Jan 24 '07  | Jan 25 '07   |  |
| 306  | Pipelaying   | 2 days   | Jan 26 '07  | Jan 27 '07   |  |
| 307  | Manhole construction   | 2 days   | Jan 29 '07  | Jan 30 '07   |  |
| 308  | Backfilling  | 1 day    | Jan 31 '07  | Jan 31 '07   | ■  |
| 309  | Drainage MHS18.4 to MHS18.3, DN150                           | 7 days   | Feb 1 '07   | Feb 8 '07    |  |
| 310  | Excavation   | 2 days   | Feb 1 '07   | Feb 2 '07    |  |
| 311  | Pipelaying   | 2 days   | Feb 3 '07   | Feb 5 '07    | -  |
| 312  | Manhole construction   | 2 days   | Feb 6 '07   | Feb 7 '07    |  |
| 313  | Backfilling  | 1 day    | Feb 8 '07   | Feb 8 '07    |  |
| 314  | External Watermain Works (Chilled Water, FS/Plumbing)        | 22 days  | Jan 17 '07  | Feb 10 '07   |  |
| 315  | Area 8 (Between Main Stable 1&2/ Vet Stable & Main Stable 3) | 10 days  | Jan 17 '07  | Jan 27 '07   |  |
| 316  | Chilled watermain pipelaying                                 | 4 days   | Jan 17 '07  | Jan 20 '07   |  |
| 317  | FS/Plumbing pipelaying                                       | 3 days   | Jan 22 '07  | Jan 24 '07   |  |
| 318  | Irrigation pipelaying  | 2 days   | Jan 25 '07  | Jan 26 '07   |  |
| 319  | WSD inspection   | 1 day    | Jan 27 '07  | Jan 27 '07   |  |
| 320  | Area 9 (Along Road ST6)                                      | 10 days  | Jan 23 '07  | Feb 2 '07    |  |
| 321  | Chilled watermain pipelaying                                 | 4 days   | Jan 23 '07  | Jan 26 '07   |  |
| 322  | FS/Plumbing pipelaying                                       | 3 days   | Jan 27 '07  | Jan 30 '07   | <b>-</b>   |
| 323  | Irrigation pipelaying  | 2 days   | Jan 31 '07  | Feb 1 '07    |  |
| 324  | WSD inspection   | 1 day    | Feb 2 '07   | Feb 2 '07    |  |
| 325  | Area 9 (Along Road ST7)                                      | 10 days  | Jan 27 '07  | Feb 7 '07    |  |
| 326  | Chilled watermain pipelaying                                 | 4 days   | Jan 27 '07  | Jan 31 '07   |  |
| 327  | FS/Plumbing pipelaying                                       | 3 days   | Feb 1 '07   | Feb 3 '07    |  |
| 328  | Irrigation pipelaying  | 2 days   | Feb 5 '07   | Feb 6 '07    | - T <u>k</u>   |
| 329  | WSD inspection   | 1 day    | Feb 7 '07   | Feb 7 '07    | -  |
| 330  | Area 9 (between Main Stable 3 and 4)                         | 9 days   | Feb 1 '07   | Feb 10 '07   |  |
| 331  | Chilled watermain pipelaying                                 | 3 days   | Feb 1 '07   | Feb 3 '07    |  |
| 332  | FS/Plumbing pipelaying                                       | 3 days   | Feb 5 '07   | Feb 7 '07    |  |
| 333  | Irrigation pipelaying  | 2 days   | Feb 8 '07   | Feb 9 '07    |  |
| 334  | WSD inspection   | 1 day    | Feb 10 '07  | Feb 10 '07   |  |
| 335  | Portion HKSI-2   | 70 days  | Jan 17 '07  | Apr 14 '07   |  |
| 336  | Footing for Light Mast                                       | 21 days  | Jan 17 '07  | Feb 9 '07    |  |
| 337  | Footing 1- Install holding down bolt and cast                | 9 days   | Jan 17 '07  | Jan 26 '07   |  |
| 338  | Footing 2- Install holding down bolt and cast                | 6 days   | Jan 27 '07  | Feb 2 '07    |  |
| 339  | Footing 3- Install holding down bolt and cast                | 6 days   | Jan 27 '07  | Feb 2 '07    |  |
| 340  | Footing 4- Install holding down bolt and cast                | 6 days   | Feb 3 '07   | Feb 9 '07    |  |
| 341  | External Drainage/Watermain Works                            | 70 days  | Jan 17 '07  | Apr 14 '07   |  |
| 342  | Drainage MHS18.5 to MHS18.6, DN300                           | 10 days  | Jan 17 '07  | Jan 27 '07   |  |
|      |  | Task     |             |              | Milestone  |
| 3 Ma | onths Rolling Programme_MP06                                 |          |             |              |  |
|      | Prepared: Jan 23 '07   | Split    | 101         |              |  |
|      | pa a a   | Progres  | 22          |              | ■ Project Summary Deadline   √   |

| ID   | Task Name                           | Duration     | Early Start | Early Finish | Uary   February   March   April   May   1/8  /15  /22  /29  2/5  /12  /19  /26  3/5  /12  /19  /26  4/2  4/9  /16  /23  /30  5/7  /14 | June             |
|------|-------------------------------------|--------------|-------------|--------------|---|------------------|
| 343  | Excavation                          | 2 days       | Jan 17 '07  | Jan 18 '07   | 7   | /21 /26  0/4 /11 |
| 344  | Pipelaying                          | 3 days       | Jan 19 '07  | Jan 22 '07   |   |                  |
| 345  | Manhole construction                | 4 days       | Jan 23 '07  | Jan 26 '07   |   |                  |
| 346  | Backfilling                         | 1 day        | Jan 27 '07  | Jan 27 '07   |   |                  |
| 347  | Drainage MHS18.6 to MHS18.7, DN300  | 10 days      | Jan 19 '07  | Jan 30 '07   | 7   |                  |
| 348  | Excavation                          | 2 days       | Jan 19 '07  | Jan 20 '07   |   |                  |
| 349  | Pipelaying                          | 3 days       | Jan 22 '07  | Jan 24 '07   |   |                  |
| 350  | Manhole construction                | 4 days       | Jan 25 '07  | Jan 29 '07   |   |                  |
| 351  | Backfilling                         | 1 day        | Jan 30 '07  | Jan 30 '07   |   |                  |
| 352  | Drainage MHS18.7 to MHS17.2, DN225  | 10 days      | Jan 22 '07  | Feb 1 '07    |   |                  |
| 353  | Excavation                          | 2 days       | Jan 22 '07  | Jan 23 '07   |   |                  |
| 354  | Pipelaying                          | 3 days       | Jan 24 '07  | Jan 26 '07   |   |                  |
| 355  | Manhole construction                | 4 days       | Jan 27 '07  | Jan 31 '07   | 7   |                  |
| 356  | Backfilling                         | 1 day        | Feb 1 '07   | Feb 1 '07    | 7   |                  |
| 357  | Drainage MHS17.2 to MHS17.3, DN225  | 10 days      | Jan 24 '07  | Feb 3 '07    | 7   |                  |
| 358  | Excavation                          | 2 days       | Jan 24 '07  | Jan 25 '07   |   |                  |
| 359  | Pipelaying                          | 3 days       | Jan 26 '07  | Jan 29 '07   |   |                  |
| 360  | Manhole construction                | 4 days       | Jan 30 '07  | Feb 2 '07    |   |                  |
| 361  | Backfilling                         | 1 day        | Feb 3 '07   | Feb 3 '07    | 7   |                  |
| 362  | Drainage MHS18.5 to MHS18.2, DN300  | 10 days      | Feb 1 '07   | Feb 19 '07   | 7   |                  |
| 363  | Excavation                          | 2 days       | Feb 1 '07   | Feb 2 '07    |   |                  |
| 364  | Pipelaying                          | 3 days       | Feb 3 '07   | Feb 6 '07    | 7   |                  |
| 365  | Manhole construction                | 4 days       | Feb 7 '07   | Feb 10 '07   |   |                  |
| 366  | Backfilling                         | 1 day        | Feb 19 '07  | Feb 19 '07   | 7   |                  |
| 367  | Drainage MHS18.2 to MHS18.1, DN375  | 10 days      | Feb 3 '07   | Feb 21 '07   | 7   |                  |
| 368  | Excavation                          | 2 days       | Feb 3 '07   | Feb 5 '07    | 7   |                  |
| 369  | Pipelaying                          | 3 days       | Feb 6 '07   | Feb 8 '07    |   |                  |
| 370  | Manhole construction                | 4 days       | Feb 9 '07   | Feb 20 '07   | 7   |                  |
| 371  | Backfilling                         | 1 day        | Feb 21 '07  | Feb 21 '07   | 7   |                  |
| 372  | Drainage MHS18.1 to CP (Ex), DN225  | 10 days      | Feb 6 '07   | Feb 23 '07   | 7   |                  |
| 373  | Excavation                          | 2 days       | Feb 6 '07   | Feb 7 '07    | 7   |                  |
| 374  | Pipelaying                          | 3 days       | Feb 8 '07   | Feb 10 '07   | 7   |                  |
| 375  | Manhole construction                | 4 days       | Feb 19 '07  | Feb 22 '07   | 7   |                  |
| 376  | Backfilling                         | 1 day        | Feb 23 '07  | Feb 23 '07   | 7   |                  |
| 377  | Drainage MHS18.1 to MHS18.11, DN150 | 10 days      | Feb 8 '07   | Feb 26 '07   |   |                  |
| 378  | Excavation                          | 2 days       | Feb 8 '07   | Feb 9 '07    | 7   |                  |
| 379  | Pipelaying                          | 3 days       | Feb 10 '07  | Feb 20 '07   |   |                  |
| 380  | Manhole construction                | 4 days       | Feb 21 '07  | Feb 24 '07   | 7   |                  |
|      | 1                                   | <del>'</del> | <u> </u>    | !            |   |                  |
| 2 R# | antha Dalling Draggers MD00         | Task         |             |              | Milestone External Tasks  |                  |
|      | onths Rolling Programme_MP06        | Split        |             |              | Summary External Milestone  |                  |
| Date | Prepared: Jan 23 '07                | Progre       |             |              | Project Summary Deadline  |                  |
|      |                                     | J            |             |              | · •   |                  |

| ID   | Task Name   | Duration | Early Start | Early Finish | uary   February   March   April   May   June   1/8   /15   /22   /29   2/5   /12   /19   /26   3/5   /12   /19   /26   4/2   4/9   /16   /23   /30   5/7   /14   /21   /28   6/4   /11   |
|------|---|----------|-------------|--------------|--|
| 381  | Backfilling   | 1 day    | Feb 26 '07  | Feb 26 '07   |  |
| 382  | Watermain Works at Area 7                                 | 10 days  | Jan 23 '07  | Feb 2 '07    |  |
| 383  | Excavation  | 2 days   | Jan 23 '07  | Jan 24 '07   |  |
| 384  | Pipelaying  | 3 days   | Jan 25 '07  | Jan 27 '07   |  |
| 385  | Manhole construction                                      | 4 days   | Jan 29 '07  | Feb 1 '07    |  |
| 386  | Backfilling   | 1 day    | Feb 2 '07   | Feb 2 '07    |  |
| 387  | Watermain Works at Area 6                                 | 20 days  | Feb 1 '07   | Mar 2 '07    |  |
| 388  | Divert existing site access                               | 1 day    | Feb 1 '07   | Feb 1 '07    | ,  |
| 389  | Excavation works  | 3 days   | Feb 2 '07   | Feb 5 '07    |  |
| 390  | Watermain connection works (pipelaying, thrustblocks etc) | 12 days  | Feb 6 '07   | Feb 26 '07   |  |
| 391  | WSD Inspection  | 1 day    | Feb 27 '07  | Feb 27 '07   |  |
| 392  | Backfilling & make good ex. road                          | 3 days   | Feb 28 '07  | Mar 2 '07    |  |
| 393  | Grass Training Arena                                      | 48 days  | Feb 19 '07  | Apr 14 '07   |  |
| 394  | Site clearance on existing log compound                   | 6 days   | Feb 19 '07  | Feb 24 '07   |  |
| 395  | Sub soil drain installation                               | 12 days  | Feb 26 '07  | Mar 10 '07   |  |
| 396  | Geotextile + subbase                                      | 6 days   | Mar 12 '07  | Mar 17 '07   | <u> </u>   |
| 397  | 20mm aggregate + bituminous layer                         | 12 days  | Mar 19 '07  | Mar 31 '07   |  |
| 398  | Compacted sand mixture                                    | 12 days  | Apr 2 '07   | Apr 14 '07   |  |
| 399  | Portion HKSI-3  | 78 days  | Jan 17 '07  | Apr 24 '07   |  |
| 400  | Storm Drainage STM1 to S.12.21A to S12.21 (exist) DN850   | 10 days  | Jan 17 '07  | Jan 27 '07   |  |
| 401  | Excavation  | 2 days   | Jan 17 '07  | Jan 18 '07   | , state of the sta |
| 402  | Pipelaying  | 8 days   | Jan 19 '07  | Jan 27 '07   |  |
| 403  | Manhole construction                                      | 8 days   | Jan 19 '07  | Jan 27 '07   |  |
| 404  | Foul Drainage FTM1 to F12.24, DN750                       | 7 days   | Jan 29 '07  | Feb 5 '07    |  |
| 405  | Pipelaying  | 5 days   | Jan 29 '07  | Feb 2 '07    |  |
| 406  | Manhole construction                                      | 5 days   | Jan 29 '07  | Feb 2 '07    | The state of the s |
| 407  | Backfilling   | 2 days   | Feb 3 '07   | Feb 5 '07    |  |
| 408  | Foul Drainage F12.21A to F12.22, DN300                    | 8 days   | Jan 17 '07  | Jan 25 '07   |  |
| 409  | Excavation  | 5 days   | Jan 17 '07  | Jan 22 '07   |  |
| 410  | Pipelaying  | 3 days   | Jan 19 '07  | Jan 22 '07   | , ————————————————————————————————————   |
| 411  | Manhole construction                                      | 3 days   | Jan 19 '07  | Jan 22 '07   |  |
| 412  | Backfilling   | 3 days   | Jan 23 '07  | Jan 25 '07   |  |
| 413  | Foul Drainage F12.21A to F12.21, DN300                    | 54 days  | Jan 26 '07  | Apr 5 '07    |  |
| 414  | Excavation  | 6 days   | Jan 26 '07  | Feb 1 '07    |  |
| 415  | Pipelaying  | 3 days   | Feb 2 '07   | Feb 5 '07    | <u> </u>   |
| 416  | Manhole construction                                      | 3 days   | Feb 6 '07   | Feb 8 '07    |  |
| 417  | Backfilling   | 3 days   | Feb 9 '07   | Feb 19 '07   | 7 <u> </u>   |
| 418  | Foul Drainage F12.21 to F12.20, DN300                     | 15 days  | Feb 20 '07  | Mar 8 '07    |  |
|      |   | Task     |             |              | Milestone  |
|      | onths Rolling Programme_MP06                              | Split    |             |              | Summary External Milestone   |
| Date | Prepared: Jan 23 '07                                      | Progres  |             |              | Project Summary Deadline   |
|      |   | 1 Togres |             |              | - 1 Tojon Sammary Deadmine   |

| ID   | Task Name                                | Duration | Early Start       | Early Finish | uary         February         March         April         May         June           1/8 /15 /22 /29 /25 /12 /19 /26 /3/5 /12 /19 /26 /3/5 /12 /19 /26 /3/5 /12 /19 /26 /3/5 /12 /19 /26 /3/5 /12 /19 /26 /3/5 /12 /19 /26 /3/5 /12 /19 /26 /3/5 /12 /19 /26 /3/5 /19 /19 /26 /3/5 /3/5 /3/5 /3/5 /3/5 /3/5 /3/5 /3/  |
|------|--|----------|-------------------|--------------|---|
| 419  | Excavation                               | 6 days   | Feb 20 '07        | Feb 26 '07   | 1/0   1/3   2/2   2/3   2/3   1/2   1/3   2/2   3/3 |
| 420  | Pipelaying                               | 3 days   | Feb 27 '07        | Mar 1 '07    |   |
| 421  | Manhole construction                     | 3 days   | Mar 2 '07         | Mar 5 '07    |   |
| 422  | Backfilling                              | 3 days   | Mar 6 '07         | Mar 8 '07    |   |
| 423  | Foul Drainage F12.20 to F11.6, DN300     | 24 days  | Mar 9 '07         | Apr 5 '07    |   |
| 424  | Excavation                               | 12 days  | Mar 9 '07         | Mar 22 '07   |   |
| 425  | Pipelaying                               | 12 days  | Mar 16 '07        | Mar 29 '07   |   |
| 426  | Manhole construction                     | 3 days   | Mar 30 '07        | Apr 2 '07    |   |
| 427  | Backfilling                              | 3 days   | Apr 3 '07         | Apr 5 '07    |   |
| 428  | Foul Drainage F11.5 to F11.6, DN300      | 15 days  | Jan 23 '07        | Feb 8 '07    |   |
| 429  | Excavation                               | 6 days   | Jan 23 '07        | Jan 29 '07   |   |
| 430  | Pipelaying                               | 3 days   | Jan 30 '07        | Feb 1 '07    |   |
| 431  | Manhole construction                     | 3 days   | Feb 2 '07         | Feb 5 '07    |   |
| 432  | Backfilling                              | 3 days   | Feb 6 '07         | Feb 8 '07    |   |
| 433  | Foul Drainage F11.5 to F11.4, DN300      | 20 days  | Feb 9 '07         | Mar 10 '07   |   |
| 434  | Excavation                               | 10 days  | Feb 9 '07         | Feb 27 '07   |   |
| 435  | Pipelaying                               | 10 days  | Feb 21 '07        | Mar 3 '07    |   |
| 436  | Manhole construction                     | 3 days   | Mar 5 '07         | Mar 7 '07    | 1 1   |
| 437  | Backfilling                              | 3 days   | Mar 8 '07         | Mar 10 '07   |   |
| 438  | Foul Drainage F11.4 to F11.3, DN300      | 16 days  | Mar 12 '07        | Mar 29 '07   |   |
| 439  | Excavation                               | 6 days   | Mar 12 '07        | Mar 17 '07   |   |
| 440  | Pipelaying                               | 6 days   | Mar 16 '07        | Mar 22 '07   |   |
| 441  | Manhole construction                     | 3 days   | Mar 23 '07        | Mar 26 '07   |   |
| 442  | Backfilling                              | 3 days   | Mar 27 '07        | Mar 29 '07   | <u> </u>  |
| 443  | Foul Drainage F11.3 to F11.2, DN300      | 22 days  | Mar 30 '07        | Apr 24 '07   |   |
| 444  | Excavation                               | 12 days  | Mar 30 '07        | Apr 12 '07   |   |
| 445  | Pipelaying                               | 12 days  | Apr 4 '07         | Apr 17 '07   |   |
| 446  | Manhole construction                     | 3 days   | Apr 18 '07        | Apr 20 '07   |   |
| 447  | Backfilling                              | 3 days   | Apr 21 '07        | Apr 24 '07   |   |
| 448  | Portion HKSI-4                           | 118 days | Jan 17 '07        | Jun 11 '07   |   |
| 449  | Foundation Works- 40m Light Mast         | 70 days  | Jan 17 '07        | Apr 14 '07   |   |
| 450  | Soil Investigation                       | 4 days   | Jan 17 '07        | Jan 20 '07   |   |
| 451  | Soil Investigation Pile Cap B            | 2 days   | Jan 17 '07        | Jan 18 '07   |   |
| 452  | Soil Investigation Pile Cap A            | 4 days   | Jan 17 '07        | Jan 20 '07   |   |
| 453  | Soil Investigation Pile Cap D            | 4 days   | Jan 17 '07        | Jan 20 '07   |   |
| 454  | Minipiles Drilling                       | 70 days  | Jan 17 '07        | Apr 14 '07   |   |
| 455  | Pile Cap C - minipile drilling           | 16 days  | Jan 17 '07        | Feb 3 '07    |   |
| 456  | Pile Cap B - minipile drilling           | 24 days  | Jan 19 '07        | Feb 22 '07   |   |
|      |  | T1       |                   |              | Milestone   |
| 3 M  | onths Rolling Programme_MP06             | Task     |                   |              | Milestone External Tasks  |
|      | Prepared: Jan 23 '07                     | Split    | 111               |              | Summary External Milestone  |
| Date | ι ιεραι <del>ε</del> α. Jan 23 <i>Ul</i> | Progres  | ss $\blacksquare$ |              | Project Summary Deadline  |

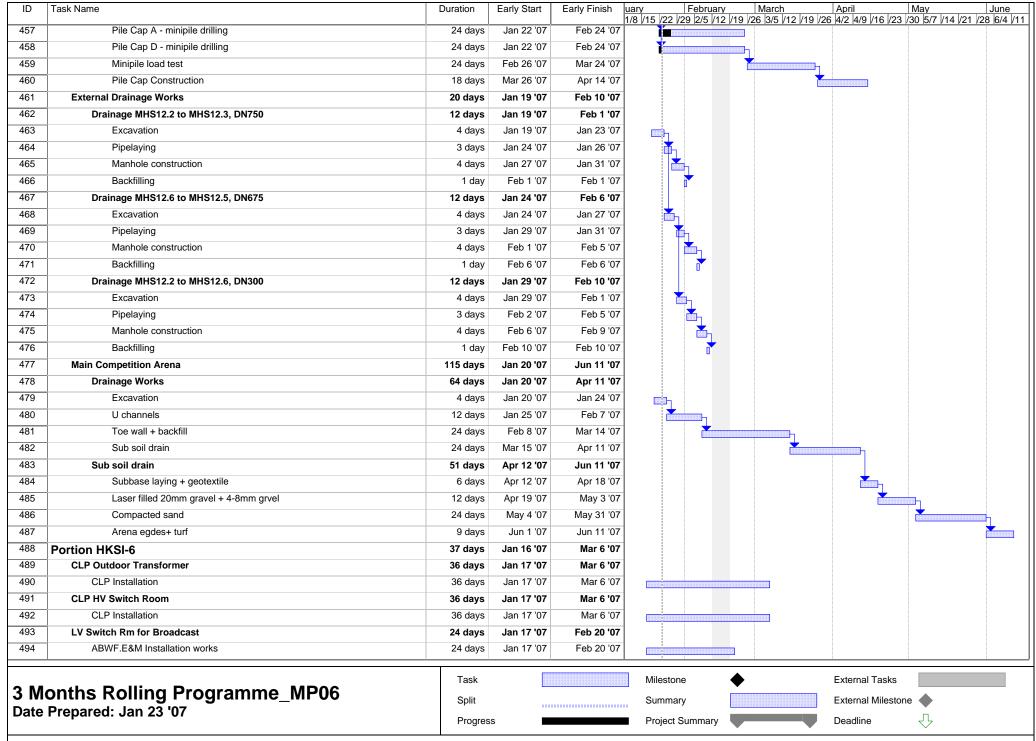

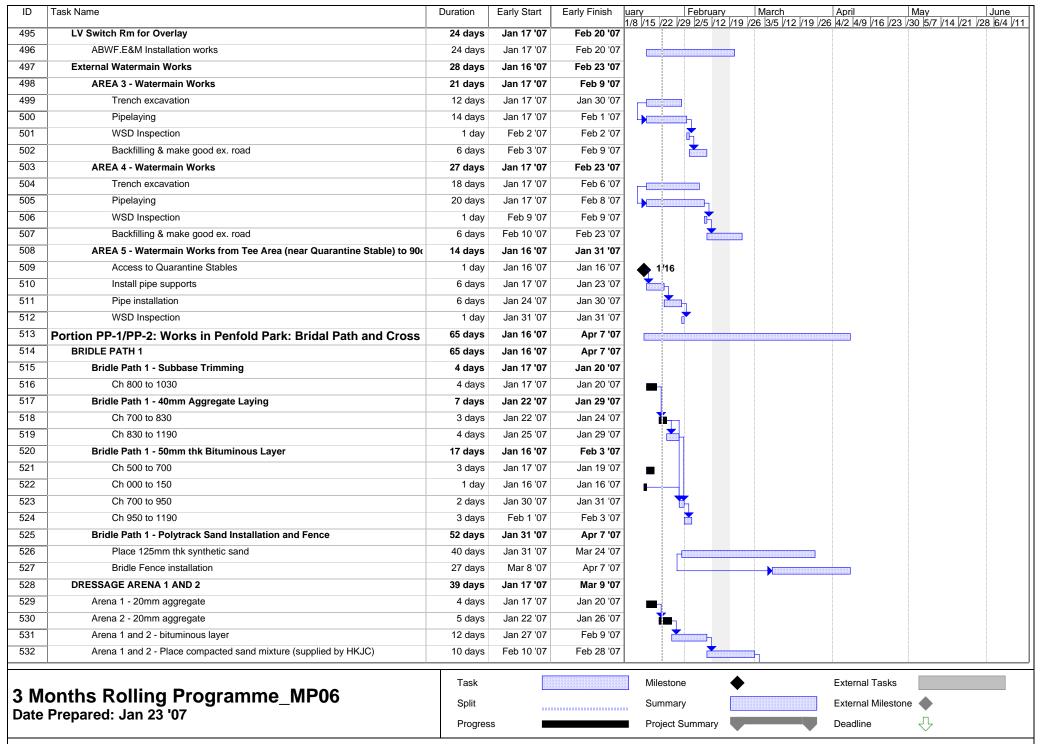

| ID   | Task Name   | Duration | Early Start | Early Finish | uary Februar                | y March<br>2  /19  /26  3/5  /12  /19  /2 | April                    | May                                     | June<br>28 6/4 /11 |
|------|---|----------|-------------|--------------|-----------------------------|---|--------------------------|---|--------------------|
| 533  | Arena fence and gate installation                 | 8 days   | Mar 1 '07   | Mar 9 '07    | 1/0 / 10 //22 //29  2/3 / 1 | 2 / 13 / 20   5/3 / 12 / 13 / 2           | .0 14/2 14/3 / 10 / 23 / | 30   3/1   y 1 <del>4</del>   y 21   y. | 20 0/4 /11         |
|      |   |          |             |              | -                           | ·   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   |          |             |              |                             |   |                          |   |                    |
|      |   | Task     |             |              | Milestone                   | •   | External Tasks           |   |                    |
| 3 M  | onths Rolling Programme_MP06 Prepared: Jan 23 '07 | Split    |             |              | Summary                     | <b>~</b>                                  | External Mileston        | • <b>•</b>                              |                    |
| Date | Prepared: Jan 23 '07                              | Progres  |             |              | ■ Project Summary           |   | Deadline                 | $\bigcirc$                              |                    |
|      |   | 1.09.00  |             |              |                             | <b>*</b>                                  |                          |   | 15 of 15           |

Appendix B

Monitoring Schedule for September and October 2007

### **Monitoring Schedule - September 2007**

|        |                 |                 | September 2007   |                                  |                    |                  |
|--------|-----------------|-----------------|------------------|----------------------------------|--------------------|------------------|
| Sunday | Monday          | Tuesday         | Wednesday        | Thursday                         | Friday             | Saturday         |
|        |                 |                 |                  |                                  |                    | 1                |
| 2      | 3               | Site Inspection | 5                | 6                                | 7 Noise Monitoring | 8                |
| 9      | Landscape Audit | 11              | 12               | Site Inspection Noise Monitoring | 14                 | 15               |
| 16     | Site Inspection | Landscape Audit | Noise Monitoring | 20                               | 21                 | 22               |
| 23     | Site Inspection | 25              | 26               | 27                               | 28                 | Noise Monitoring |
| 30     |                 |                 |                  |                                  |                    |                  |

### **Tentative Monitoring Schedule - October 2007**

|        |                                  |                  | October 2007     |                  |                                  |          |
|--------|----------------------------------|------------------|------------------|------------------|----------------------------------|----------|
| Sunday | Monday                           | Tuesday          | Wednesday        | Thursday         | Friday                           | Saturday |
|        | 1                                | 2                | 3                | Site Inspection  | Noise Monitoring Landscape Audit | 6        |
| 7      | Site Inspection                  | 9                | Noise Monitoring | 11               | 12                               | 13       |
| 14     | 15                               | Noise Monitoring | Site Inspection  | 18               | 19                               | 20       |
| 21     | Site Inspection  Landscape Audit | 23               | 24               | Noise Monitoring | 26                               | 27       |
| 28     | Site Inspection                  | 30               | 31               |                  |                                  |          |
|        |                                  |                  |                  |                  |                                  |          |

Appendix C

Environmental Mitigation Implementation Schedule

| EIA<br>Ref. | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address  | Who to implement the measures? | Location of the measures       | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve?  |
|-------------|--|---|--------------------------------|--------------------------------|---------------------------------|----------------|--|
| S3.8        | The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation  • Any excavated of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where | Good construction site<br>practices to control the<br>dust impact at the<br>nearby sensitive<br>receivers to within the | Contractor                     | Entire<br>construction<br>site | Construction<br>stage           | <b>*</b>       | <ul> <li>To control the<br/>dust impact to<br/>within the<br/>HKAQO and<br/>TM-EIA criteria</li> </ul> |
|             | practicable within 24 hours of the excavation or unloading; <ul> <li>Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads or streets:</li> </ul>   | relevant criteria.  |                                |                                |                                 | ✓              | (Ref. 1-hr and<br>24hr TSP<br>levels are 500<br>μ gm <sup>-3</sup> and 260                             |
|             | <ul> <li>The load of dusty materials on a vehicle leaving a construction<br/>site should be covered entirely by impervious sheeting to ensure that<br/>the dusty materials do not leak from the vehicle;</li> </ul>  |   |                                |                                |                                 | <b>✓</b>       | $\mu$ gm <sup>-3</sup> , respectively)   |
|             | Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point.  |   |                                |                                |                                 | <b>√</b>       |  |
|             | should be paved with concrete, bituminous materials or hardcores;  • When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as  |   |                                |                                |                                 | <b>√</b>       |  |
|             | practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period;   |   |                                |                                | * 1                             |                |  |
|             | The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials;  |   |                                |                                |                                 | v              |  |
|             | Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet;   |   |                                |                                |                                 | <b>√</b>       |  |
|             | Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of   |   |                                |                                |                                 | N/A            |  |
|             | the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding;  • Any skip hoist for material transport should be totally enclosed by   |   |                                |                                |                                 | <b>√</b>       |  |
|             | impervious sheeting;   |   |                                |                                |                                 | *              |  |

| EIA<br>Ref. | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address   | Who to implement the measures? | Location of the measures       | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve?         |
|-------------|--|--|--------------------------------|--------------------------------|---------------------------------|----------------|---|
| S3.8.2      | <ul> <li>The Contract shall adopt adequate measures to mitigate the odour impact to acceptable level:</li> <li>A sanitary environment will always be maintained in the stable area. The current waste management practices will be extended to cover the new stable area at HKSI. Detailed design of stable will cater for the health, safety and environmental protection considerations in accordance with the HKJC policy and practice;</li> <li>Regular maintenance of the odour removal system, such as carbon filter system will be carried out to maintain the odour removal efficiency; and</li> <li>Enclosed containers, similar to those at the existing stables near HKSI, will be provided for the stockpiling of waste.</li> </ul>  | minimize the potential odour impact to nearby sensitive receivers            | Contractor                     | Stables                        | Operational<br>Phase            | N/A            | TM-EIA, Annex 4  5 odour units based on averaging time of 5 seconds |
| S4.8.1.1    | 1) Use of good site practices to limit noise emissions by considering the following:  • only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme;  • machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;  • plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs;  • silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works;  • mobile plant should be sited as far away from NSRs as possible and practicable;  • material stockpiles, mobile container site officer and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities. | Control construction<br>airborne noise by<br>means of good site<br>practices | Contractor                     | Entire<br>construction<br>site | Construction<br>stage           | * * * * * *    | Noise Control<br>Ordinance  |

| EIA<br>Ref. | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address                         | Who to implement the measures? | Location of the measures       | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve?   |
|-------------|--|--|--------------------------------|--------------------------------|---------------------------------|----------------|---|
| S4.8.1.2    | 2) Install temporary hoarding of 2.4m high located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period. | Reduce the construction<br>noise levels at low-level<br>zone of NSRs through<br>partial screening. | Contractor                     | Entire<br>construction<br>site | Construction<br>stage           | <b>*</b>       | Noise Control Ordinance Annex 5, TM-EIA Hoarding should have no openings and a superficial surface density of at least 14kg/m².   |
| S4.8.1.3    | 3) Install movable noise barriers (typically density @14kg/m²), acoustic mat close to noisy plants including air compressor, water pump, hand-held breaker and pipe pile rigs.   | Screen the noisy plant items to be used at all construction sites                                  | Contractor                     | Entire<br>construction<br>site | Construction<br>stage           |                | Noise Control Ordinance     Annex 5, TM-EIA     75dB(A) for residential premises and 70dB(A) for schools during daytime     The movable barrier should achieve at least 5dB(A) and the full enclosure should be designed to achieve 10dB(A) |

| EIA<br>Ref. | Recommended Mitigation Measures   | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address                   | Who to implement the measures? | Location of the measures   | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve?  |
|-------------|---|--|--------------------------------|--|---------------------------------|----------------|--|
| S4.8.1.4    | 4) Liaise with the school representative(s) including, but not limited to Hong Kong Institute of Vocational Education (Shatin), Jockey Club Ti-1 College, International Christian School – Elementary and Leung Kui Kau Primary School to obtain the examination schedule and avoid noisy construction activities during school examination period. | Schedule the construction works outside school examination periods to less intrusive periods | Contractor                     | Construction sites near the schools such as Hong Kong Institute of Vocational Education (Shatin), Jockey Club Ti-1 College, International Christian School – Elementary and Leung Kui Kau Primary School | Construction<br>stage           | N/A            | Noise Control Ordinance Annex 5, TM-EIA To comply with the daytime construction noise criterion of 65dB(A) at school during the examination periods, |
| \$4.8.1.5   | 5) Select "Quiet plants" which comply with the BS 5228 Part 1 or TM standards.  | Reduce the noise levels of plant items   | Contractor                     | Entire<br>construction<br>site   | Construction stage              | <b>√</b>       | Noise Control<br>Ordinance & its<br>TM     Annex 5, TM-<br>EIA   |
| S4.8.1.6    | 6) Sequencing operation of construction plant equipment.  | Operate sequentially within the same work site to reduce the construction airborne noise     | Contractor                     | Entire<br>construction<br>site where<br>practicable  | Construction<br>stage           | <b>√</b>       | Noise Control<br>Ordinance     Annex 5, TM-<br>EIA   |
| S4.8.4.1    | The Louvres should be orientated away from adjacent NSRs where possible, preferably onto Sha Tin Racecourse which are less sensitive.   | Control operational noise from fixed sources   | Designers                      | E&M plant items  | Design stage                    | ~              | • HKPSG  |
| \$4.8.4.1   | <ol> <li>Adequate direct noise mitigation measures including silencers,<br/>acoustic louvers, acoustic enclosures should be allowed for in the<br/>design.</li> </ol>   | Control operational noise from fixed sources   | Designers                      | E&M plant<br>items   | Design stage                    | <b>/</b>       | • HKPSG  |
| \$4.8.4.2   | A cluster of small power rated loudspeakers should be used instead of a few large power rated loudspeakers  | Control operational noise from fixed sources   | Designers                      | PA system  | Design stage                    | <b>*</b>       | • HKPSG  |

| EIA<br>Ref. | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address   | Who to implement the measures? | Location of the measures       | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve?                  |
|-------------|--|--|--------------------------------|--------------------------------|---------------------------------|----------------|--|
| S4.8.4.2    | 4) Directional loudspeakers should be used and orientated them to point towards the audience and away from the nearby noise sensitive receivers  | Control operational<br>noise from fixed<br>sources   | Designers                      | PA system                      | Design stage                    | <b>√</b>       | • HKPSG  |
| S5.6.1      | 1) Follow the site practices outlined in ProPECC PN 1/94 as far as practicable in order to minimise surface runoff and the chance of erosion, and to reduce any suspended solids prior to discharge.   | Good site practice to control construction water quality   | Contractor                     | Entire<br>construction<br>site | Construction stage              | <b>√</b> :     | Requirements     laid down in     ProPECC PN     1/94                        |
| S5.6.1      | Sewage Effluent  1) Portable chemical toilets and sewage holding tanks are recommended for handling the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance. | Control sewage effluent<br>arising from the sanitary<br>facilities provided for the<br>on-site construction<br>workforce | Contractor                     | On-site sanitary facilities    | Construction stage              | •              | ProPECC PN 1/94  Water Pollution Control Ordinance  Waste Disposal Ordinance |

| EIA<br>Ref. | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address   | Who to implement the measures? | Location of the measures       | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve? |
|-------------|--|--|--------------------------------|--------------------------------|---------------------------------|----------------|---|
| S5.6.1      | <ul> <li>Construction Runoff and Site Drainage</li> <li>At the start of site establishment (including the barging facility), perimeter cut-off drains to direct off-site water around the site should be constructed with internal drainage works and erosion and sedimentation control facilities implemented. Channels (both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities.</li> </ul>                   | Control construction runoff and erosion from site surface, drainage channel, stockpiles, barging facility, wheel washing facilities, etc to minimize water quality during construction stage | Contractor                     | Entire<br>construction<br>site | Construction<br>stage           | <b>✓</b>       | ProPECC PN 1/94 Water Pollution Control Ordinance           |
|             | • The dikes or embankments for flood protection should be implemented around the boundaries of earthwork areas. Temporary ditches should be provided to facilitate the runoff discharge into an appropriate watercourse, through a site/sediment trap. The sediment/silt traps should be incorporated in the permanent drainage channels to enhance deposition rates.  |  |                                |                                |                                 | ~              |   |
|             | <ul> <li>The design of efficient silt removal facilities should be based on<br/>the guidelines in Appendix A1 of ProPECC PN 1/94, which states<br/>that the retention time for silt/sand traps should be 5 minutes under<br/>maximum flow conditions.</li> </ul>   |  |                                |                                |                                 | ~              |   |
|             | • Construction works should be programmed to minimize surface excavation works during the rainy seasons (April to September). All exposed earth areas should be completed and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means. |  |                                |                                |                                 | <b>√</b>       |   |
|             | The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all trafficked areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows.  |  |                                |                                |                                 | *              |   |
|             | All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas.  |  |                                |                                |                                 | ~              | ,   |

| EIA<br>Ref.  | Recommended Mitigation Measures   | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address | Who to implement the measures? | Location of the measures | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve? |
|--------------|---|--|--------------------------------|--------------------------|---------------------------------|----------------|---|
|              | <ul> <li>Measures should be taken to minimise the ingress of site<br/>drainage into excavations. If the excavation of trenches in wet<br/>periods is necessary, they should be dug and backfilled in short<br/>sections wherever practicable. Water pumped out from trenches or<br/>foundation excavations should be discharged into storm drains via<br/>silt removal facilities.</li> </ul>   |  |                                |                          |                                 |                |   |
|              | <ul> <li>Open stockpiles of construction materials (for example,<br/>aggregates, sand and fill material) of more than 50 m3 should be<br/>covered with tarpaulin or similar fabric during rainstorms. Measures<br/>should be taken to prevent the washing away of construction<br/>materials, soil, silt or debris into any drainage system.</li> </ul>   |  |                                |                          |                                 | <b>✓</b>       |   |
|              | Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.  |  |                                |                          |                                 | <b>~</b>       |   |
|              | <ul> <li>Precautions to be taken at any time of year when rainstorms are<br/>likely, actions to be taken when a rainstorm is imminent or<br/>forecasted, and actions to be taken during or after rainstorms are<br/>summarised in Appendix A2 of ProPECC PN 1/94. Particular<br/>attention should be paid to the control of silty surface runoff during<br/>storm events, especially for areas located near steep slopes.</li> </ul>  |  |                                |                          | 3.4                             | <b>✓</b>       |   |
|              | • All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing bay should be provided at every construction site exit. Wash-water should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road should be paved with sufficient backfall toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains. |  |                                |                          |                                 | *              |   |
|              | Oil interceptors should be provided in the site drainage system downstream of any oil/fuel pollution sources. The oil interceptors should be emptied and cleaned regularly to prevent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for the oil interceptors to prevent flushing during heavy rain.   |  |                                |                          |                                 | N/A            |   |
| G:\env\proje | ct\24469-70\reports\EM&A\Monthly\2007-09\appendices\implementation schedule.doc   |  |                                |                          |                                 |                | Page 7 of 16  |

| EIA<br>Ref. | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address               | Who to implement the measures?            | Location of the measures       | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve?   |
|-------------|--|--|---|--------------------------------|---------------------------------|----------------|---|
|             | Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts. Requirements for solid waste management are detailed in Section 6 of the EIA Report.  |  |   |                                |                                 | <b>*</b>       |   |
|             | All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearby.  |  |   |                                |                                 | *              |   |
| S5.6.2.1    | A low flow interceptor drainage system should be constructed to intercept the first foul flush and convey it to a storage tank from where it is pumped to the foul drainage system. The catchment area of the low flow interceptor drainage covers the area of Main Stable Complex. Sand traps will also be provided at the stable to prevent sand from being conveyed into the pipe system. | Control surface runoff   | Scheme<br>designers<br>and/or<br>Operator | Drainage<br>system             | Design and/or operational stage | В              | TM-water     Water Pollution Control Ordinance  |
| \$5.6.2.2   | A new 450mm public gravity sewer should be constructed along the pathway of the Shing Mun River and be connected to the existing 450mm public sewer at the southeastern corner of HKSI to collect the sewage from the new Stable Complex and the low flow interceptor system.  | Control sewage collection  | Scheme<br>designers                       | Sewage<br>System               | Design stage                    | В              | Water Pollution<br>Control<br>Ordinance     TM-water  |
| \$6.5.1.1   | 1) The requirements as recommended in ETWB TC 15/2003 Waste Management on Construction Sites and its latest version, and other relevant guidelines, should be included in the Particular Specification as appropriate.   | Develop waste<br>management strategies<br>and minimize<br>construction waste<br>disposal | Scheme<br>Designer                        | Entire<br>construction<br>site | Design stage                    | <b>✓</b>       | Waste Disposal<br>Ordinance     ETWB TC<br>15/2003  |
| S6.5.1.1    | 2) Prior to the commencement of construction work, the Contractor should prepare a WMP to provide an overall framework for waste management and reduction.   | Develop waste<br>management and<br>reduction strategies                                  | Contractor                                | Entire<br>construction<br>site | Construction<br>stage           | <b>√</b> :     | Waste Disposal Ordinance     ETWB TC     15/2003     Wste Disposal (Chemical Waste)     (General)     Regulation     ETWBTC     34/2002 |

| EIA<br>Ref.                 | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address  | Who to implement the measures? | Location of the measures | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve?  |
|-----------------------------|--|---|--------------------------------|--------------------------|---------------------------------|----------------|--|
| \$6.5.1.2<br>&<br>\$6.5.1.3 | Construction and Demolition Material Opportunity for re-using of fill material for back filling should be optimized.  Excavated materials that cannot be recycled should be transported to public filling areas.  Careful design, planning and good site management can minimise over-ordering and waste materials such as concrete, mortars and cement grouts. The design of formwork should maximise the use of standard wooden panels so that high reuse levels can be achieved. Alternatives such as steel formwork or plastic fencing should be considered to increase the potential for reuse.  The contractor should recycle as much as possible of the construction waste on-site. Proper segregation of wastes on site will increase the feasibility of recycling certain components of the waste stream by recycling contractors. Concrete and masonry can be used as general fill and steel reinforcement bars can be used by scrap steel mills. Different areas should be designated for such segregation and storage wherever site conditions permit.  Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement.  Surplus artificial hard materials should be delivered to Tuen Mun Area 38 recycling plant or its successor for recycling into subsequent useful products.  On-site sorting and segregation facility of all type of wastes is considered as one of the best practice in waste management and hence, should be implemented in all projects generating construction waste. The sorted public fill and construction & demolition (C&D) waste should be disposed to public filling areas and landfills, respectively. | Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal | Contractor                     | Entire construction site | Construction stage              |                | Land     (Miscellaneous     Provisions)     Ordinance     Waste     Disposal     Ordinance     ETWB TC     15/2003 |

| EIA<br>Ref. | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address | Who to implement the measures? | Location of the measures | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve?                    |
|-------------|--|--|--------------------------------|--------------------------|---------------------------------|----------------|--|
|             | Make provisions in the Contract documents to allow and promote<br>the use of recycled aggregates where appropriate.  |  |                                |                          |                                 |                |  |
|             | <ul> <li>Implement a trip-ticket system for each works contract to ensure<br/>that the disposal of C&amp;D materials are properly documented and<br/>verified.</li> </ul>  |  |                                |                          |                                 | ✓              |  |
|             | • Implement an enhanced Waste Management Plan similar to ETWB TC(W) No. 15/2003 – "Waste Management on Construction Sites" to encourage on-sitting sorting of C&D materials and to minimize their generation during the course of construction.  |  |                                |                          |                                 | *              |  |
| S6.5.1.4    | Chemical Waste   | Control the chemical   | Contractor                     | Entire                   | Construction                    |                | Waste  |
|             | Chemical waste that is produced, as defined by Schedule 1 of<br>the Waste Disposal (Chemical Waste) (General) Regulation, should<br>be handled in accordance with the Code of Practice on the<br>Packaging, Labelling and Storage of Chemical Wastes.  | waste and ensure<br>proper storage,<br>handling and disposal.              |                                | construction<br>site     | stage                           | N/A            | Disposal<br>(Chemical<br>Waste) General)<br>Regulation<br>• Code of            |
|             | Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; have a capacity of less than 450 liters unless the specification has been approved by the EPD; and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation.   |  |                                |                          |                                 | <b>*</b>       | Practice on the<br>Packaging,<br>Labelling and<br>Storage of<br>Chemical Waste |
|             | The storage area for chemical wastes should be clearly labelled and used solely for the storage of chemical waste; enclosed on at least 3 sides; have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20 % of the total volume of waste stored in that area, whichever is the greatest; have adequate ventilation; covered to prevent rainfall entering; and arranged so that incompatible materials are adequately separated. |  |                                |                          |                                 | <b>✓</b>       |  |
|             | Disposal of chemical waste should be via a licensed waste collector; be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre which also offers a chemical waste collection service and can supply the necessary storage containers; or be to a reuser of the waste, under approval from the EPD.  |  |                                |                          |                                 | N/A            |  |

| EIA<br>Ref. | Recommended Mitigation Measures   | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address                  | Who to implement the measures? | Location of the measures       | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve? |
|-------------|---|---|--------------------------------|--------------------------------|---------------------------------|----------------|---|
| S6.5.1.6    | <ul> <li>Sewage</li> <li>Adequate numbers of portable toilets should be provided for the workers. The portable toilets should be maintained in a state, which will not deter the workers from utilizing these portable toilets. Night soil should be collected by licensed collectors regularly.</li> </ul>     | Proper handling of<br>sewage from worker to<br>avoid odour, pest and<br>litter impacts      | Contractor                     | Entire<br>construction<br>site | Construction<br>stage           | <b>✓</b>       | Waste Disposal<br>Ordinance                                 |
| S6.5.1.5    | General Refuse  General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes.  | Minimize production of<br>the general refuse and<br>avoid odour, pest and<br>litter impacts | Contractor                     | Entire<br>construction<br>site | Construction stage              | ·              | Waste Disposal<br>Ordinance                                 |
|             | • A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law.                         |   |                                |                                |                                 | *              |   |
|             | • Aluminium cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible.   |   |                                |                                | * (                             | ·              |   |
|             | Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor. In addition, waste separation facilities for paper, aluminium cans, plastic bottles etc., should be provided. |   |                                |                                |                                 | ·              |   |
|             |   |   |                                |                                |                                 |                |   |

| Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address   | Who to implement the measures?  | Location of the measures  | When to implement the measures?   | Implementation  | What requirements or standards for the measures to achieve?   |
|--|--|---|---|---|---|---|
| Municipal Waste     Recycling bins will be provided at shops and food service locations to collect cardboard containers. Personnel in office will be provided with bins to recycle office paper.   | Storage and handing of waste   | Operator  | Entire project<br>site  | Operational<br>stage  | В   | Waste Disposal<br>Ordinance   |
| Aluminium can recycling bins will be placed at prominent locations for collection  |  | II  |   |   | В   |   |
| Recycling bins for plastic bottle recovery should be set up at prominent places to facilitate visitors' participation in material recovery activities.   |  |   |   |   | В   |   |
| • The landscaping works will generate a certain amount of grass clippings, leaves, bush and tree trimmings. However, the handling capacity of the existing Sha Ling composting facility is limited and is currently composting livestock wastes. The facility is unlikely to be able to handle the green waste generated from the Project site. Should there be a market or facility which could process the green waste arising from the Project site, the establishment of a recycling programme for green waste should be considered. |  | 1   |   |   | N/A   |   |
| The venue operator should make arrangements with the laser printer toner cartridge suppliers to collect and recycle used toner cartridges for laser printers to avoid disposal of the cartridge at landfills as far as practicable.  |  |   |   |   | В   |   |
| Waste from Stables     Waste from horse stables (mainly the horse manure) would be collected on a regular basis following HKJC's sanitary practices.   | Storage and handing of waste   | Operator  | Entire project<br>site  | Operational<br>stage  | В   | Waste Disposal<br>Ordinance   |
|  | <ul> <li>Municipal Waste</li> <li>Recycling bins will be provided at shops and food service locations to collect cardboard containers. Personnel in office will be provided with bins to recycle office paper.</li> <li>Aluminium can recycling bins will be placed at prominent locations for collection</li> <li>Recycling bins for plastic bottle recovery should be set up at prominent places to facilitate visitors' participation in material recovery activities.</li> <li>The landscaping works will generate a certain amount of grass clippings, leaves, bush and tree trimmings. However, the handling capacity of the existing Sha Ling composting facility is limited and is currently composting livestock wastes. The facility is unlikely to be able to handle the green waste generated from the Project site. Should there be a market or facility which could process the green waste arising from the Project site, the establishment of a recycling programme for green waste should be considered.</li> <li>The venue operator should make arrangements with the laser printer toner cartridge suppliers to collect and recycle used toner cartridges for laser printers to avoid disposal of the cartridge at landfills as far as practicable.</li> <li>Waste from Stables</li> <li>Waste from horse stables (mainly the horse manure) would be</li> </ul> | Recommended Mitigation Measures  Municipal Waste  Recycling bins will be provided at shops and food service locations to collect cardboard containers. Personnel in office will be provided with bins to recycle office paper.  Aluminium can recycling bins will be placed at prominent locations for collection  Recycling bins for plastic bottle recovery should be set up at prominent places to facilitate visitors' participation in material recovery activities.  The landscaping works will generate a certain amount of grass clippings, leaves, bush and tree trimmings. However, the handling capacity of the existing Sha Ling composting facility is limited and is currently composting livestock wastes. The facility is unlikely to be able to handle the green waste generated from the Project site. Should there be a market or facility which could process the green waste arising from the Project site, the establishment of a recycling programme for green waste should be considered.  The venue operator should make arrangements with the laser printer toner cartridge suppliers to collect and recycle used toner cartridges for laser printers to avoid disposal of the cartridge at landfills as far as practicable.  Waste from Stables  Waste from horse stables (mainly the horse manure) would be | Recommended Mitigation Measures  Recommended Measures & Main Concerns to address  Municipal Waste  Recycling bins will be provided at shops and food service locations to collect cardboard containers. Personnel in office will be provided with bins to recycle office paper.  Aluminium can recycling bins will be placed at prominent locations for collection  Recycling bins for plastic bottle recovery should be set up at prominent places to facilitate visitors' participation in material recovery activities.  The landscaping works will generate a certain amount of grass clippings, leaves, bush and tree trimmings. However, the handling capacity of the existing Sha Ling composting facility is limited and is currently composting livestock wastes. The facility is unlikely to be able to handle the green waste generated from the Project site. Should there be a market or facility which could process the green waste arising from the Project site, the establishment of a recycling programme for green waste should be considered.  The venue operator should make arrangements with the laser printer toner cartridge suppliers to collect and recycle used toner cartridges for laser printers to avoid disposal of the cartridge at landfills as far as practicable.  Waste from Natables  Waste from horse stables (mainly the horse manure) would be | Recommended Mitigation Measures    Recommended Measures & Main Concerns to address   Implement the measures | Recommended Mitigation Measures  Recommended Measures & Main Concerns to address  Municipal Waste  Recycling bins will be provided at shops and food service locations to collect cardboard containers. Personnel in office will be provided with bins to recycle office paper.  Aluminium can recycling bins will be placed at prominent locations for collection  Recycling bins for plastic bottle recovery should be set up at prominent places to facilitate visitors' participation in material recovery activities.  The landscaping works will generate a certain amount of grass clippings, leaves, bush and tree trimmings. However, the handling capacity of the existing Sha Ling composting facility is limited and is currently composting livestock wastes. The facility is unlikely to be able to handle the green waste generated from the Project site. Should there be a market or facility which could process the green waste arising from the Project site, the establishment of a recycling programme for green waste should be considered.  The venue operator should make arrangements with the laser printer toner cartridge suppliers to collect and recycle used toner cartridges for laser printers to avoid disposal of the cartridge at landfills as far as practicable.  Waste from Stables  Storage and handing of waste  Storage and handing of Operator site in the measures?  Location of the measures?  Entire project site.  Implement the measures?  Departure of the measures?  Operational stage | Recommended Mitigation Measures  Recommended Mitigation Measures  Recommended Mitigation Measures  Municipal Waste  Recycling bins will be provided at shops and food service locations to collect cardboard containers. Personnel in office will be provided with bins to recycle office paper.  Aluminium can recycling bins will be placed at prominent locations for collection  Recycling bins for plastic bottle recovery should be set up at prominent places to facilitate visitors' participation in material recovery activities.  The landscaping works will generate a certain amount of grass clippings, leaves, bush and tree trimmings. However, the handling capacity of the existing Sha Ling composting facility is limited and is currently composting livestock wastes. The facility is unlikely to be able to handle the green waste generated from the Project site. Should there be a market or facility which could process the green waste arising from the Project site, the establishment of a recycling programme for green waste should be considered.  The venue operator should make arrangements with the laser printer toner cartridges puppliers to collect and recycle used toner cartridges for laser printers to avoid disposal of the cartridge at landfills as far as practicable.  Waste from Notes stables (mainly the horse manure) would be  Waste from horse stables (mainly the horse manure) would be |

| EIA<br>Ref.    | Recommended Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address | Who to implement the measures? | Location of the measures | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve? |
|----------------|--|--|--------------------------------|--------------------------|---------------------------------|----------------|---|
| S9.3 &<br>S9.7 | An Independent Environmental Checker needs to be employed as per the EM&A Manual.  | Control EM&A<br>Performance  | Project<br>Proponent           | All construction sites   | Construction stage              | *              | EIAO Guidance     Note No.4/2002     TM-EIAO                |
|                | 2) Establish a telephone hotline which enables the public to raise any matters of concern regarding the project such as complaints, comments, suggestions or requests for information. |  |                                |                          |                                 | <b>✓</b>       | • TWI-EIAO  |
| S9.5           | An Environmental Team needs to be employed as per the EM&A Manual.   | Perform environmental monitoring & auditing                                | Contractor                     | All construction sites   | Construction stage              | <b>~</b>       | • EIAO Guidance<br>Note No.4/2002                           |
|                | 2) Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures.   |  |                                |                          |                                 | ~              | • TM-EIAO   |
|                | 3) An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with.              |  |                                |                          |                                 | ✓.             |   |
|                | 4) Real-time reporting of monitoring data for the Project through a dedicated internet website need to be provided and maintained by the Environmental Team                            |  |                                |                          |                                 | *              |   |

Note: ✓ - Implemented

O - Partially implemented
B - To be implemented
N/A - Not applicable

| EP<br>Condition<br>Ref | Mitigation Measures   | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address | Who to implement the measures?       | Location of the measures | When to implement the measures? | Implementation | What requirements or standards for the measures to achieve? |
|------------------------|---|--|--------------------------------------|--------------------------|---------------------------------|----------------|---|
| deasures to            | Mitigate Construction Noise Impact  |  |                                      |                          |                                 |                |   |
| 3.1                    | Noise reduction measures in the form of movable barrier or site hoarding shall be adopted to alleviate the construction noise impacts. A purpose built temporary noise barriers of 2.4 m high shall be built along the site boundaries. Movable barrier with a wooden or steel frame of vertical/cantilever type shall be adopted and located close to the noise generating part of Powered Mechanical Equipment (PME). The barrier material shall have a surface mass of not less than 14 kg/m² on a skid footing with 25mm thick internal sound absorptive lining to achieve the maximum screening effect | To mitigate construction noise impact                                      | Contractor                           | Entire project<br>site   | Construction<br>Stage           | <b>~</b>       | Environmental<br>Permit No. EP-<br>236/2006                 |
| 3.2                    | The permit holder shall liaise with the school representative(s) including but not limited to Hong Kong Institute of Vocational Education (Shatin), Jockey Club Ti-I College, International Christian School – Elementary and Leung Kui Kau Primiary School to obtain the examination schedule to avoid noisy construction activities during the school examination period  |  | Contractor /<br>Project<br>Proponent |                          | Construction<br>Stage           | <b>√</b>       |   |
| 3.3                    | The Permit Holder shall ensure the implementation of noise mitigation measures are in full compliance with the details as set out in Conditions 3.1 above   |  | Project<br>Proponent                 | Entire project<br>site   | Construction<br>Stage           | <b>V</b>       |   |
| 3.4                    | No percussive piling shall be carried out   |  | Contractor                           | Entire project site      | Construction<br>Stage           | ~              |   |
| Measures to            | Mitigate Landscape Impact   | ·  |                                      |                          |                                 |                |   |
| 3.5                    | All tree felling and transplanting activities shall strictly be conducted in accordance with the Tree Survey Schedule at Appendix 1   | To mitigate landscape impact   | Contractor                           | Entire project site      | Construction<br>Stage           | <b>V</b>       | Environmental<br>Permit No. EP-<br>236/2006                 |

| EP<br>Condition<br>Ref | Mitigation Measures   | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address | Who to implement the measures? | Location of the measures | When to implement the measures? | Implementation   | What requirements or standards for the measures to achieve? |
|------------------------|---|--|--------------------------------|--------------------------|---------------------------------|--|---|
| 3.6                    | The Permit Holder shall submit three sets of the landscape impact mitigation plan for the Olympic mode (including the details of tree felling, transplanting and retention, methodology for transplanting and protection of retained trees, tree compensation plan and landscape plan) to the Director for approval at least three months before commencement of construction. Compensation of trees shall be in a ratio of at least 2 new trees for every tree felled. Similarly the landscape impact mitigation plan for the reinstatement works shall be submitted at least three months before commencement of reinstatement works. Implementation of all works in the landscape impact mitigation plans shall be certified by the IEC and as built drawings shall be deposited with the Director upon completion of the works. |  | Project<br>Proponent           |                          | Construction<br>Stage           | O (The landscape impact mitigation plan for Olympic Mode was submitted 3 months before commencement of construction) |   |
| Measures to            | Mitigate Operational Noise Impact   |  | li                             |                          |                                 |  |   |
| 4.1                    | A limiter device shall be installed and operated in the Public Address System to ensure full control of setting the maximum output sound level during the Test Event, Olympic Event and Paralympic Event  | To mitigate operational noise impact                                       | Operator                       | Entire project<br>site   | Operational<br>Stage            | 1  |   |
| 4.2                    | Directional loudspeakers shall be used for the Public Address System  |  | Operator                       | Entire project site      | Operational Stage               | *  |   |
| Measures to            | Mitigate Odour Impact   |  |                                |                          |                                 |  |   |
| 4.3                    | Two rounds of odour patrol shall be conducted; one during the Test Event and the other just prior to the Olympic Event after the arrival of all competition horses in order to ascertain the odour impact   | To mitigate odour impact   | Project<br>Proponent           | Entire project<br>site   | Operational<br>Stage            | O<br>(Odour patrol<br>during Test Event<br>has been<br>conducted)  |   |
| Measures to            | Mitigate Water Quality Impact   | ·  |                                |                          | *                               | *  |   |
| 4.4                    | A low flow interceptor drainage system shall be constructed and in operation to intercept surface runoff.   | To mitigate water quality impact   | Contractor                     | Entire project site      | Construction<br>Stage           | ~  |   |
| 4.5                    | A new sewer shall be constructed along the pathway of the Shing Mun River to collect the sewage from the low flow interceptor drainage system.  |  | Contractor                     | Entire project site      | Construction<br>Stage           | 1  |   |

| EP<br>Condition<br>Ref | Mitigation Measures  | Objectives of the<br>Recommended<br>Measures & Main<br>Concerns to address | Who to implement the measures?     | Location of the measures | When to implement the measures? | Implementation   | What requirements or standards for the measures to achieve? |
|------------------------|--|--|------------------------------------|--------------------------|---------------------------------|--|---|
| <u>Measures to</u>     | Mitigate Glare Impact  |  |                                    |                          |                                 |  |   |
| 4.6                    | The use of the floodlights at the Main Arena shall be restricted to competition hours only   | To mitigate glare impact   | Operator                           | Entire project site      | Operational<br>Stage            | <b>✓</b>   |   |
| 4.7                    | Each floodlight unit at the Main Arena shall have a built-in antiglare baffle and visor shield to limit the glare  |  | Operator                           | Entire project site      | Operational<br>Stage            | ·  |   |
| 4.8                    | Each floodlight unit at the Main Arena shall not be equipped with metal halide lamps of more than 2000W.   |  | Operator                           | Entire project site      | Operational<br>Stage            | <b>V</b>   |   |
| 4.9                    | The illuminance level of floodlight units shall be reduced to that of the existing racecourse after the 2008 Olympic and Paralympic Equestrian Events. The Permit Holder shall submit information on the existing illumination level of the existing racecourse before construction of the Main Arena for this purpose |  | Operator /<br>Project<br>Proponent | Entire project<br>site   | Operational<br>Stage            | O (The existing illumination level of the racecourse was included in the Baseline Environmental Monitoring Report submitted before construction stage) |   |

Note: ✓

✓ - Implemented

O - Partially implemented
B - To be implemented
N/A - Not applicable

## Appendix D

Calibration certificates of noise monitoring equipment

#### **Summary of Equipment Calibration Details**

| Equipment Type                                | Model                                    | Serial No.         | Last Calibration Date | Next Calibration<br>Date |
|---|--|--------------------|-----------------------|--------------------------|
|   | D.:" -1 0 1/ 0000                        | 2320694<br>2274284 | 1 Sep 2007            | 31 August 2008           |
| Integrating sound level meter with microphone | - Brüel & Kjær 2238<br>Brüel & Kjær 4188 | 2320696<br>2274286 | 1 Sep 2007            | 31 August 2008           |
|   |  | 2320707<br>2179479 | 1 Sep 2007            | 31 August 2008           |
| Acoustical calibrator                         | Brüel & Kjær 4231                        | 2314016            | 1 Sep 2007            | 31 August 2008           |

Issued by: Brüel & Kjær UK Ltd.

Date of Issue: OIFEB 2007

Certificate Number: 15784



0174

## Brüel & Kjær

Bedford House, Rutherford Close, Stevenage.

Hertfordshire. SG1 2ND

Telephone: 01438 739100 Fax.: 01438 739199

E-Mail: ukservice@bksv.com

Page 1 of 4 pages

Approved signatory

Name: A.M. HAMM

## **CALIBRATION OF MULTI FREQUENCY CALIBRATOR TYPE 4226**

("Free Field and Random" version)

Client:

ARUP ACOUSTICS PARKIN HOUSE

8 ST. THOMAS STREET WINCHESTER SO23 9HE

Calibrator Type 4226,

S/No: 1531372

With Coupler UA0915,

S/No: 1531372

Client Inventory Number:

Manufacturer:

Brüel & Kjær

Equipment Received on:

23 JAN 2007

Calibration Date:

01 FEB 2007

Brüel & Kjær Reference No:

1-97267724

Measurement Method

The Calibration was performed to Laboratory Procedure TWI-103.

Sound pressure level in the 1/2 inch coupler of the calibrator was measured with a laboratory grade condenser microphone Type 4180, used as a working standard, calibrated by the National Physical Laboratory.

This certificate is issued in accordance with the laboratory accreditation requirements of the United Kingdom Accreditation Service. It provides traceability of measurement to recognised national standards, and to units of measurement realised at the National Physical Laboratory or other recognised national standards laboratories. This certificate may not be reproduced other than in full, except with the prior written approval of the issuing laboratory.

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

15784

Page 2 of 4 pages

The measured sound pressure was compared with that generated in the coupler of a working standard pistonphone calibrated by the National Physical Laboratory whose output was cross checked against a reference standard pistonphone, also calibrated by the National Physical Laboratory, using the same microphone and at the same ambient conditions. Appropriate corrections for atmospheric pressure conditions during calibration and for the measurement frequency and level response were taken into account.

Sound pressure level results are the mean of 5 measurements.

Results apply directly to the following settings on the calibrator, pressure, linear, calibration, 94dB, microphone group a, b, c.

Results for frequency and distortion are the result of a single measurement.

Results for 104 and 114dB are only at 125Hz, 1kHz and 8kHz, compared with the output at 94dB.

Calibration results apply at ambient conditions during the process of calibration.

Calibrations marked (Not UKAS Accredited) in this certificate have been included for completeness.

### **CALIBRATION RESULTS**

4226 Settings: Linear, Pressure, 94dB, Microphone Group c.

| Frequency<br>Setting Hz | Sound Pressure<br>Level in dB re 20µPa | Frequency<br>Hz       | Distortion<br>%       |
|-------------------------|--|-----------------------|-----------------------|
|                         |  | (Not UKAS Accredited) | (Not UKAS Accredited) |
| 31.5                    | 94.13                                  | 31.63                 | 0.5                   |
| 63                      | 94.07                                  | 63.13                 | 0.2                   |
| 125                     | 94.04                                  | 125.9                 | 0.2                   |
| 250                     | 94.02                                  | 251.3                 | 0.2                   |
| 500                     | 94.00                                  | 502.5                 | 0.2                   |
| 1k                      | 94.04                                  | 1.005 k               | 0.2                   |
| 2k                      | 94.02                                  | 1.979 K               | 0.4                   |
| 4k                      | 94.07                                  | 3.957k                | 0.2                   |
| 8k                      | 94.16                                  | 7.915k                | 0.3                   |
| 12.5k                   | 94.08                                  | 12.66 k               | 0.2                   |

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

15784

Page 3 of 4 pages

#### Expanded uncertainty of calibration:

Sound Pressure Level:

 $\pm 0.15$ dB from 31.5Hz to 2kHz,

±0.20dB at 4kHz and 8kHz,

±0.25dB at 12.5kHz

Frequency:

±1 last significant digit reported.

Distortion:

 $\pm 0.3\%$  distortion.

The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor k=2, providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with UKAS requirements.

### **ADDITIONAL TESTS**

#### Sound Pressure Levels at Settings of 94, 104 and 114 dB

| Frequency | Difference<br>104-94dB | Difference<br>114-94dB |
|-----------|------------------------|------------------------|
| 125 Hz    | 9.99                   | 19.97                  |
| 1kHz      | 10.00                  | 19.98                  |
| 8kHz      | 9.96                   | 19.93                  |

Result of a single measurement, expanded uncertainty ±0.15dB

#### Inverted "A" Weighting, Readings Relative to 1kHz in dB

| Frequency<br>Hz | 31.5   | 63     | 125    | 250   | 500   | 1 k | 2 k  | 4 k   | 8 k   | 12.5 k |
|-----------------|--------|--------|--------|-------|-------|-----|------|-------|-------|--------|
| Target<br>Value | + 39.4 | + 26.2 | + 16.1 | + 8.6 | + 3.2 | 0   | -1.2 | - 1.0 | + 1.1 | + 4.3  |
| Reading         | 39.6   | 26.2   | 16.1   | 8.6   | 3.2   | 0.0 | -1.2 | -1.0  | 1.2   | 4.3    |

Target values according to BS EN 60651 - 1994 - results of a single measurement, values rounded to  $0.1 \, dB$ , expanded uncertainty  $\pm 0.3 dB$ .

UKAS Accredited Calibration Laboratory No. 0174

Certificate Number

15784

Page 4 of 4 pages

#### Free Field and Random settings

|             |                    |               | Random             |                                       |                    |                    |                    |               |
|-------------|--------------------|---------------|--------------------|---------------------------------------|--------------------|--------------------|--------------------|---------------|
|             | Micro<br>Gro       | -             |                    | Microphone Microphone Group b Group c |                    | Microphone Group b |                    |               |
| Freq.<br>Hz | Target<br>Value dB | Reading<br>dB | Target<br>Value dB | Reading<br>dB                         | Target<br>Value dB | Reading<br>dB      | Target<br>Value dB | Reading<br>dB |
| 250         | 0                  | 0.00          | 0                  | 0.00                                  | 0                  | 0.00               | 0                  | 0.00          |
| 500         | 0                  | 0.00          | 0                  | 0.00                                  | 0                  | 0.00               | 0                  | 0.00          |
| 1k          | +0.15              | 0.15          | +0.20              | 0.19                                  | +0.10              | 0.10               | +0.05              | 0.03          |
| 2k          | +0.50              | 0.49          | +0.45              | 0.44                                  | +0.35              | 0.34               | +0.10              | 0.09          |
| 4k          | +1.35              | 1.34          | +1.05              | 1.04                                  | +0.95              | 0.93               | +0.15              | 0.13          |
| 8k          | +4.50              | 4.47          | +2.80              | 2.78                                  | +2.60              | 2.58               | +0.40              | 0.38          |
| 12.5k       | +7.35              | 7.29          | +5.60              | 5.54                                  | +5.05              | 5.00               | +1.50              | 1.48          |

Target values as specified in the manufacturer's manual, result of a single measurement, expanded uncertainty  $\pm 0.2 dB$ .

#### Ambient conditions during calibration were:

| Atmospheric Pressure | 101.7 | kPa |
|----------------------|-------|-----|
| Temperature          | 23    |     |
| Relative Humidity    | 17    | 0/_ |

Checked by:





Level 5 Festival Walk 80 Tat Chee Avenue Kowloon Tong, Kowloon HONG KONG

AAc Certificate No. 2007004

Fax: +852 2268 3950

Tel: +852 2268 3216

#### CERTIFICATE OF CONFORMITY

**Description of Test Instrument** Type No Serial No Brüel & Kjær Sound Level Meter Kit 2238 2320694 Brüel & Kjær 1/2 " Microphone Kit 4188 2274284

Date of Test: 01 September 2007

Carried out by: Raymond Liu

Approved by: William Ng

Signature:

Signature:

**Ambient Conditions During Test** 

Atmospheric Pressure: 1KPa Air Temperature: 21°C Relative Humidity: 58%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

Description of Reference Calibrator Type No Serial No Brüel & Kjær Multi Frequency Calibrator 4226 1531372 Brüel & Kiær Coupler UA0915 1531372

Certificate of Calibration Serial No.

15784

By Brüel & Kjær (UK) Ltd Calibration Date:

01 February 2007

NAMAS Accredited Calibration Laboratory No.

0174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

#### Footnote:

Arup Acoustics is not a registered NAMAS accredited calibration laboratory. This certificate is for internal use only (unless otherwise authorised) and is part of Arup Acoustics development and commitment to QC and QA procedures.



Level 5 Festival Walk 80 Tat Chee Avenue Kowloon Tong, Kowloon HONG KONG AAc Certificate No. 2007005

Fax: +852 2268 3950

Tel: +852 2268 3216

#### **CERTIFICATE OF CONFORMITY**

Description of Test InstrumentType NoSerial NoBrüel & Kjær Sound Level Meter Kit22382320696Brüel & Kjær ½ " Microphone Kit41882274286

Date of Test:

01 September 2007

Carried out by: Raymond Liu

Approved by:

William Ng

Signature: faymond

Signature:

Who no

**Ambient Conditions During Test** 

Atmospheric Pressure: 1KPa
Air Temperature: 21°C
Relative Humidity: 58%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

Description of Reference CalibratorType NoSerial NoBrüel & Kjær Multi Frequency Calibrator42261531372Brüel & Kjær CouplerUA09151531372

Certificate of Calibration Serial No.

15784

01 February 2007

By Brüel & Kjær (UK) Ltd Calibration Date: NAMAS Accredited Calibration Laboratory No.

0174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

#### Footnote:

Arup Acoustics is not a registered NAMAS accredited calibration laboratory. This certificate is for internal use only (unless otherwise authorised) and is part of Arup Acoustics development and commitment to QC and QA procedures.



Level 5 Festival Walk 80 Tat Chee Avenue Kowloon Tong, Kowloon HONG KONG AAc Certificate No. 2007006

Fax: +852 2268 3950

Tel: +852 2268 3216

#### **CERTIFICATE OF CONFORMITY**

Description of Test InstrumentType NoSerial NoBrüel & Kjær Sound Level Meter Kit22382320707Brüel & Kjær ½ " Microphone Kit41882179479

Date of Test:

01 September 2007

Carried out by: Raymond Liu

Approved by: William Ng

Signature: Raymond

Signature:

Will No

**Ambient Conditions During Test** 

Atmospheric Pressure: 1KPa
Air Temperature: 21°C
Relative Humidity: 58%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

Description of Reference CalibratorType NoSerial NoBrüel & Kjær Multi Frequency Calibrator42261531372Brüel & Kjær CouplerUA09151531372

Certificate of Calibration Serial No.

15784

By Brüel & Kjær (UK) Ltd Calibration Date:

01 February 2007

NAMAS Accredited Calibration Laboratory No.

0174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

#### Footnote:

Arup Acoustics is not a registered NAMAS accredited calibration laboratory. This certificate is for internal use only (unless otherwise authorised) and is part of Arup Acoustics development and commitment to QC and QA procedures.



Level 5 Festival Walk 80 Tat Chee Avenue Kowloon Tong, Kowloon HONG KONG AAc Certificate No. 2007001

Fax: +852 2268 3950

Tel: +852 2268 3216

#### **CERTIFICATE OF CONFORMITY**

**Description of Test Instrument** 

Type No

Serial No

Bruel & Kjaer 4231Acoustic Calibrator

4231

2314016

Date of Test:

01 September 2007

Carried out by: Raymond Liu

Approved by:

William Ng

Signature: Kommond

Signature:

With My

#### **Ambient Conditions During Test**

Atmospheric Pressure: 1KPa
Air Temperature: 21°C
Relative Humidity: 58%

This document is to certify that the above Test Instrumentation did conform to the manufacturer's original specification on the date of the test. Any adjustments that were required to bring the instrumentation back into specification are duly noted in this document. The tests were carried out using the reference calibrator described below.

Description of Reference CalibratorType NoSerial NoBrüel & Kjær Multi Frequency Calibrator42261531372Brüel & Kjær CouplerUA09151531372

Certificate of Calibration Serial No. 15784

By Brüel & Kjær (UK) Ltd Calibration Date: 01 February 2007

NAMAS Accredited Calibration Laboratory No. 0174

The reference calibrator, Type 4226, has traceable calibration back to National Measurement Standards. As such it is used as Arup Acoustics own 'Primary Standard' and is used only for controlled laboratory calibration tests on all sound measuring equipment owned by Arup Acoustics.

#### Footnote:

Arup Acoustics is not a registered NAMAS accredited calibration laboratory. This certificate is for internal use only (unless otherwise authorised) and is part of Arup Acoustics development and commitment to QC and QA procedures.

Appendix E

Detailed noise monitoring results

## **Details of Noise Impact Monitoring**

|        |           | NSR | Time p | eriods | Weather   | Avg. wind   | Noise Level dB(A) |                 |                 | Influencing factors/ |
|--------|-----------|-----|--------|--------|-----------|-------------|-------------------|-----------------|-----------------|----------------------|
| Month  | Date      | No. | Start  | Finish | condition | speed (m/s) | $L_{eq}$          | L <sub>10</sub> | L <sub>90</sub> | Site condition       |
| Jun-07 | 07-Jun-07 | NM1 | 14:40  | 15:10  | Fine      | 1.1         | 64.7              | 67.1            | 62.1            | Normal Operation     |
| Jun-07 | 07-Jun-07 | NM2 | 14:00  | 14:30  | Fine      | 0.7         | 63.2              | 64.9            | 61.3            | Normal Operation     |
| Jun-07 | 07-Jun-07 | NM3 | 15:35  | 16:05  | Fine      | 1.4         | 61.5              | 63.9            | 58.7            | Normal Operation     |
| Jun-07 | 14-Jun-07 | NM1 | 14:43  | 15:13  | cloudy    | 1.8         | 63.5              | 65.0            | 61.0            | Normal Operation     |
| Jun-07 | 14-Jun-07 | NM2 | 14:00  | 14:30  | cloudy    | 2.5         | 62.9              | 64.0            | 61.5            | Normal Operation     |
| Jun-07 | 14-Jun-07 | NM3 | 15:38  | 16:08  | cloudy    | 1.4         | 61.3              | 63.1            | 59.0            | Normal Operation     |
| Jun-07 | 23-Jun-07 | NM1 | 9:45   | 10:15  | Sunny     | 1.2         | 62.8              | 64.0            | 61.5            | Normal Operation     |
| Jun-07 | 23-Jun-07 | NM2 | 9:00   | 9:30   | Sunny     | 1.7         | 62.5              | 63.7            | 61.0            | Normal Operation     |
| Jun-07 | 23-Jun-07 | NM3 | 10:50  | 11:20  | Sunny     | 1.5         | 60.4              | 62.8            | 58.5            | Normal Operation     |
| Jun-07 | 28-Jun-07 | NM1 | 14:43  | 15:13  | cloudy    | 2.5         | 63.7              | 64.4            | 61.0            | Normal Operation     |
| Jun-07 | 28-Jun-07 | NM2 | 14:00  | 14:30  | cloudy    | 2.1         | 63.0              | 64.3            | 61.5            | Normal Operation     |
| Jun-07 | 28-Jun-07 | NM3 | 15:50  | 16:20  | cloudy    | 1.9         | 61.2              | 63.7            | 60.0            | Normal Operation     |
| Jul-07 | 04-Jul-07 | NM1 | 14:45  | 15:15  | Fine      | 1.7         | 63.3              | 64.7            | 61.5            | Normal Operation     |
| Jul-07 | 04-Jul-07 | NM2 | 14:10  | 14:40  | Fine      | 1.4         | 62.5              | 64.0            | 62.0            | Normal Operation     |
| Jul-07 | 04-Jul-07 | NM3 | 15:55  | 16:25  | Fine      | 1.1         | 61.7              | 63.6            | 61.0            | Normal Operation     |
| Jul-07 | 12-Jul-07 | NM1 | 15:00  | 15:30  | Sunny     | 1.2         | 62.0              | 63.6            | 59.7            | Normal Operation     |
| Jul-07 | 12-Jul-07 | NM2 | 14:20  | 14:50  | Sunny     | 1.1         | 65.5              | 67.7            | 62.9            | Normal Operation     |
| Jul-07 | 12-Jul-07 | NM3 | 16:05  | 16:35  | Sunny     | 0.9         | 62.1              | 63.5            | 61.5            | Normal Operation     |
| Jul-07 | 19-Jul-07 | NM1 | 10:10  | 10:40  | Sunny     | 1.3         | 62.7              | 64.0            | 60.5            | Normal Operation     |
| Jul-07 | 19-Jul-07 | NM2 | 9:30   | 10:00  | Sunny     | 1.5         | 64.5              | 65.4            | 63.0            | Normal Operation     |
| Jul-07 | 19-Jul-07 | NM3 | 11:10  | 11:40  | Sunny     | 1.1         | 62.6              | 63.9            | 61.7            | Normal Operation     |
| Jul-07 | 26-Jul-07 | NM1 | 14:50  | 15:20  | Sunny     | 1.6         | 63.3              | 65.0            | 61.0            | Normal Operation     |
| Jul-07 | 26-Jul-07 | NM2 | 14:00  | 14:30  | Sunny     | 1.9         | 64.1              | 66.5            | 61.5            | Normal Operation     |
| Jul-07 | 26-Jul-07 | NM3 | 15:50  | 16:20  | Sunny     | 1.4         | 61.1              | 63.0            | 60.0            | Normal Operation     |

## **Details of Noise Impact Monitoring**

|        |           | NSR | Time p | eriods | Weather   | Avg. wind   | Noise Level dB(A) |                 |                 | Influencing factors/ |
|--------|-----------|-----|--------|--------|-----------|-------------|-------------------|-----------------|-----------------|----------------------|
| Month  | Date      | No. | Start  | Finish | condition | speed (m/s) | $L_{eq}$          | L <sub>10</sub> | L <sub>90</sub> | Site condition       |
| Aug-07 | 02-Aug-07 | NM1 | 10:30  | 11:00  | Sunny     | 1.3         | 61.8              | 62.5            | 60.5            | Normal Operation     |
| Aug-07 | 02-Aug-07 | NM2 | 9:50   | 10:20  | Sunny     | 1.6         | 64.9              | 66.5            | 62.5            | Normal Operation     |
| Aug-07 | 02-Aug-07 | NM3 | 11:30  | 12:00  | Sunny     | 2.4         | 58.7              | 60.0            | 57.0            | Normal Operation     |
| Aug-07 | 07-Aug-07 | NM1 | 14:40  | 15:10  | Fine      | 1.7         | 62.1              | 63.5            | 61.0            | Normal Operation     |
| Aug-07 | 07-Aug-07 | NM2 | 14:00  | 14:30  | Fine      | 1.8         | 64.6              | 66.0            | 63.0            | Normal Operation     |
| Aug-07 | 07-Aug-07 | NM3 | 15:35  | 16:05  | Fine      | 2.1         | 59.2              | 61.0            | 58.0            | Normal Operation     |
| Aug-07 | 16-Aug-07 | NM1 | 15:00  | 15:30  | Fine      | 1.1         | 62.6              | 64.0            | 60.5            | Normal Operation     |
| Aug-07 | 16-Aug-07 | NM2 | 14:15  | 14:45  | Fine      | 0.8         | 63.4              | 65.0            | 61.5            | Normal Operation     |
| Aug-07 | 16-Aug-07 | NM3 | 16:05  | 16:35  | Fine      | 1.3         | 60.5              | 61.5            | 58.5            | Normal Operation     |
| Aug-07 | 23-Aug-07 | NM1 | 10:10  | 10:40  | Fine      | 1.5         | 63.3              | 64.5            | 59.5            | Normal Operation     |
| Aug-07 | 23-Aug-07 | NM2 | 9:30   | 10:00  | Fine      | 0.9         | 64.1              | 65.5            | 62.5            | Normal Operation     |
| Aug-07 | 23-Aug-07 | NM3 | 11:05  | 11:35  | Fine      | 1.1         | 61.0              | 62.0            | 59.0            | Normal Operation     |
| Aug-07 | 29-Aug-07 | NM1 | 9:50   | 10:20  | Fine      | 1.2         | 64.2              | 65.0            | 60.5            | Normal Operation     |
| Aug-07 | 29-Aug-07 | NM2 | 9:15   | 9:45   | Fine      | 0.9         | 64.9              | 66.5            | 63.0            | Normal Operation     |
| Aug-07 | 29-Aug-07 | NM3 | 10:45  | 11:15  | Fine      | 0.6         | 61.5              | 63.0            | 59.5            | Normal Operation     |
| Sep-07 | 07-Sep-07 | NM1 | 13:45  | 14:15  | Fine      | 1.4         | 63.9              | 65.5            | 61.5            | Normal Operation     |
| Sep-07 | 07-Sep-07 | NM2 | 13:00  | 13:30  | Fine      | 1.2         | 64.5              | 67.0            | 63.5            | Normal Operation     |
| Sep-07 | 07-Sep-07 | NM3 | 14:40  | 15:10  | Fine      | 0.9         | 61.0              | 63.5            | 60.0            | Normal Operation     |
| Sep-07 | 13-Sep-07 | NM1 | 11:20  | 11:50  | Fine      | 1.5         | 62.9              | 64.7            | 61.1            | Normal Operation     |
| Sep-07 | 13-Sep-07 | NM2 | 10:25  | 10:55  | Fine      | 1.1         | 62.6              | 63.9            | 60.9            | Normal Operation     |
| Sep-07 | 13-Sep-07 | NM3 | 9:20   | 9:50   | Fine      | 0.7         | 60.8              | 62.5            | 58.0            | Normal Operation     |
| Sep-07 | 19/Sep/07 | NM1 | 10:00  | 10:30  | Sunny     | 1.1         | 62.5              | 63.5            | 60.0            | Normal Operation     |
| Sep-07 | 19/Sep/07 | NM2 | 9:15   | 9:45   | Sunny     | 0.9         | 63.0              | 64.5            | 61.0            | Normal Operation     |
| Sep-07 | 19/Sep/07 | NM3 | 11:15  | 11:45  | Sunny     | 0.6         | 61.1              | 62.5            | 59.0            | Normal Operation     |
| Sep-07 | 29-Sep-07 | NM1 | 10:10  | 10:40  | Fine      | 0.6         | 61.7              | 62.5            | 60.5            | Normal Operation     |
| Sep-07 | 29-Sep-07 | NM2 | 9:30   | 10:00  | Fine      | 0.9         | 62.4              | 63.5            | 61.0            | Normal Operation     |
| Sep-07 | 29-Sep-07 | NM3 | 11:00  | 11:30  | Fine      | 0.4         | 62.2              | 63.0            | 59.0            | Normal Operation     |

Appendix F

Landscape and visual monitoring and audit report

#### 1. Monitoring results

#### 1.1 Landscape and Visual

The construction of the main arena and stables has been completed. Visual impacts were greatly mitigated as the stable walls and all of the planting works in arena and stables areas have been completed. With future growth of vegetation, the impact will be further reduced. Future works to be carried out pertain to temporary overlay features.

#### 1.2 Environmental Site Auditing

Landscape and visual monitoring and site audits were carried out on 10<sup>th</sup> and 18<sup>th</sup> September 2007. Main arena, warm-up arena and stable construction works have been completed.

Most transplanted and retained trees were generally in fair condition. The Contractor shall remove all wild climbers on the transplanted trees areas and remove all dead branches of retained trees.

#### 1.3 Implementation Statuses of Landscape and Visual Impact Measures

The implementation statuses of environmental protection requirements are summarized in the following table.

Table 1.1 Implementation Statuses of Landscape and Visual Impact Measures

| EIA EM&A      |          |  | Location /  | Implementati         | - |   |   | Implementation  | Relevant<br>Legislation<br>& |  |
|---------------|----------|--|---|----------------------|---|---|---|---|------------------------------|--|
| Ref           | Ref      | Environmental Protection Measures*   | Timing  | on Agent             | С | 0 | R | Status  | Guidelines                   |  |
| ands          | cape and | d Visual Impact - Construction Phase   |   |                      |   |   |   |   | ľ                            |  |
| Table<br>7.31 | MC1      | Site offices, construction yard and holding nursery:  Site offices and the construction yard shall be decommissioned after construction.  Construction roads shall be decommissioned and landscape areas be restored to its original or newly proposed state.  The holding nursery for decorative plants at show jumps shall be decommissioned after the Olympic events. | At concealed location                               | HKJC's<br>Contractor | × |   | x | Construction: To commence. Reinstatement: To commence | Nil.                         |  |
| Table<br>7.31 | MC 2     | Height of site offices:  The height of site offices shall be controlled in order to avoid visual impacts.  | At concealed location                               | HKJC's<br>Contractor | × |   | x | Construction: Complied. Reinstatement: To commence.   |                              |  |
| Table<br>7.31 | e MC 3   | Hoarding and screening:  Where practical the site offices areas, construction yards and storage areas shall be screened with decorative hoarding or vegetation around the peripheries until the completion of relevant construction phases.  | Site offices, construction yards and storage areas. | HKJC's<br>Contractor | , | ( | x | Construction: Complied. Reinstatement To commence     |                              |  |

## 2008 Olympic Equestrian Event Landscape and Visual Impact Report – September 2007

|            |  | T            |            | Ė |   | срог | t - September 2007 |         |
|------------|--|--------------|------------|---|---|------|--------------------|---------|
| Table MC 4 | Construction plant and building        | All areas    | HKJC's     | x |   | X    | Construction:      | Nil.    |
| 7.31       | material:                              | with         | Contractor |   |   |      | Generally          |         |
|            | Shall be orderly and carefully         | constructio  |            |   |   |      | satisfactory.      |         |
|            | stored in order to appear neat and     | n plant and  |            |   |   |      |                    |         |
|            | avoid visibility from outside where    | building     |            |   |   |      | Reinstatement:     |         |
|            | practical;                             | material     |            |   |   |      | To commence        |         |
|            | Excess materials shall be              |              |            |   |   |      |                    |         |
|            | removed from site as soon as           | 180          |            |   |   |      |                    |         |
|            | practical; and                         |              |            |   |   |      |                    |         |
|            | All construction plant shall be        |              |            |   |   |      |                    |         |
|            | removed from site upon completion of   |              |            |   |   |      |                    |         |
|            | construction works.                    |              |            |   |   |      |                    |         |
|            |  |              |            |   |   |      |                    |         |
| Table MC 5 | Construction light:                    | All          | HKJC's     | х |   | x    | No construction    | Nil.    |
| 7.31       | To be oriented away from the           | construction | Contractor |   |   |      | lights at present. | 5. 3.5. |
|            | viewing location of VSRs; and          | lights       |            |   |   |      |                    |         |
|            | All construction lights shall          |              |            |   |   |      |                    |         |
|            | have frosted diffusers and reflective  |              |            |   |   |      |                    |         |
|            | covers.                                |              |            |   |   |      |                    |         |
|            |  |              |            |   |   |      |                    |         |
| Table MC 6 | Vegetation:                            | Affected     | HKJC's     | × |   | Х    |                    | Nil.    |
| 7.31       | Temporary construction sites           | vegetation   | Contractor |   |   |      | Construction:      |         |
| -          | shall be restored to standards as good | areas        |            |   |   |      | Most of the        |         |
|            | as, or better than, the original       |              |            |   |   |      | retained and       |         |
|            | condition;                             |              |            |   |   |      | transplanted       |         |
|            | The potential for soil erosion         |              |            |   |   |      | trees have been    |         |
|            | shall be reduced at the construction   |              |            |   |   |      | fenced off.        |         |
|            | stage by minimizing the extent of      |              |            |   |   |      |                    |         |
|            | vegetation disturbance on site and by  |              |            |   |   |      | No materials       |         |
|            | providing a protective cover over      |              |            |   |   |      | were stored        |         |
|            | exposed ground; and                    |              |            |   | 1 |      | under the          |         |
|            | No construction equipment or           |              |            |   |   |      | dripline of trees. |         |
|            | building materials shall be stored     |              |            |   |   |      | Complied.          |         |
|            | under the dripline of retained trees   |              |            |   |   |      |                    |         |
|            | and no vehicle movement or other       |              |            |   |   |      | Reinstatement:     |         |
|            | construction activities like washing,  | -            |            |   |   |      | To commence.       |         |
|            | concrete mixing etc shall be carried   |              |            |   |   |      |                    |         |
|            | out under the dripline of trees.       |              |            |   |   |      |                    |         |
|            | ·                                      |              |            |   |   |      |                    |         |
|            | I .                                    |              |            |   |   |      | l .                |         |

2008 Olympic Equestrian Event Landscape and Visual Impact Report – September 2007

|         |      |  |              |            |   | $\neg \tau$ | $\neg \tau$ |                      | 2.42     |
|---------|------|--|--------------|------------|---|-------------|-------------|----------------------|----------|
| Table I | MT 1 | Compensation for losses:                           | At           | HKJC's     | X |             | x           |                      | Nil.     |
| 7.31    |      | <ul> <li>The tree compensation to tree</li> </ul>  | available    | Contractor |   |             | 1           | Complied.            |          |
|         |      | loss ratio shall be 1:2; and                       | areas        |            |   |             |             |                      |          |
|         |      | <ul> <li>At least 82 new trees of light</li> </ul> | suitable for |            |   |             |             | Reinstatement:       |          |
|         |      | standard or larger size shall be                   | healthy      |            |   |             |             | To commence,         |          |
|         |      | planted.   | tree growth  |            |   |             |             |                      |          |
|         |      | <b>'</b>   |              |            |   |             |             |                      |          |
| Table   | MT 2 | The majority of compensation species               | General      | HKJC's     | x |             | х           | Construction:        | Nil.     |
| 7.31    |      | shall comprise of species that already             |              | Contractor |   |             |             | Complied.            |          |
| 7.31    |      | occurs within the LIA boundaries.                  |              |            |   |             |             |                      |          |
|         |      | Coodie Wikimi are an early                         |              |            |   | П           |             | Reinstatement:       |          |
|         |      |  |              |            |   | Н           |             | Not required.        |          |
| Table   | MTO  | Where practical, trees that require                | At           | HKJC's     | x |             | x           | Construction:        | ETWB     |
|         | MI3  | removal shall be transplanted on Site.             | available    | Contractor | 1 |             |             | Complied.            | TCW NO.  |
| 7.31    |      | removal shall be transplanted on one.              | areas        |            |   |             |             |                      | 2/2004,  |
|         |      |  | suitable for |            |   |             |             | <br>  Reinstatement: | WBTC No. |
|         |      |  | healthy      |            |   |             |             | Not required.        | 3/2006   |
|         |      | 1  | tree growth  |            |   |             |             |                      | BD PNAP  |
|         |      | 1  | liee growin  |            |   |             |             |                      | No. 267  |
|         |      |  | ۸.           | HKJC's     | + | ╁           | x           | Construction:        | Nil.     |
|         | MT 4 | Planting Works:                                    | At           | Contractor |   |             | ^           | Complied.            |          |
| 7.31    |      | <ul> <li>New trees, bamboos and</li> </ul>         | available    | Contractor |   |             |             | Complica:            |          |
|         |      | shrubs shall be planted in groups in               | areas        |            |   |             |             | Reinstatement:       |          |
|         | 1=   | order to screen visual impacts and to              | suitable for |            |   |             |             |                      |          |
|         |      | provide additional shade.                          | healthy      |            |   | 1           |             | To commence.         |          |
|         | *5   |  | tree growth  |            |   | 1           |             |                      |          |
|         |      |  | and along    |            |   | 1           |             |                      |          |
|         |      |  | approach     |            |   |             |             |                      |          |
|         |      |  | footpath     | 1          |   |             |             |                      |          |
|         |      |  |              |            | + | +           | -           |                      | WDTO No  |
| Table   | MT 5 | Tree Planting on Slopes:                           | On           | HKJC's     |   | <b>'</b>    | ×           | 11.0                 | WBTC No  |
| 7.31    | 1    | <ul> <li>New slopes with a gradient</li> </ul>     | affected     | Contracto  | r |             |             | Complied.            | 17/2000  |
|         |      | larger than 30° shall have shrub,                  | slopes       |            |   |             |             | 1                    | WBTC No  |
|         |      | groundcover or grass planting.                     |              |            |   |             |             | Reinstatement        |          |
|         |      |  |              |            |   |             |             | To commence          |          |
|         |      |  |              |            |   |             |             |                      | No. 270  |

### 2008 Olympic Equestrian Event Landscape and Visual Impact Report – September 2007

|       |      |   | Landscap     | e and Visual II | npac | ıĸ | eport – September 2007 |      |
|-------|------|---|--------------|-----------------|------|----|------------------------|------|
| Table | MT 6 | Tree Preservation:                                | At existing  | HKJC's          | x    |    | x Construction:        | Nil  |
| 7.31  |      | No tree shall be transplanted or                  | locations    | Contractor      |      |    | Tree protection        |      |
|       |      | felled without prior approval by                  | of retained  |                 |      |    | has been               |      |
|       |      | relevant Government departments;                  | trees and    |                 |      |    | recorded but           |      |
|       |      | <ul> <li>All trees that are marked for</li> </ul> | transplanta  |                 |      |    | some retained          |      |
|       |      | retention shall be fenced off with a              | tion areas,  |                 |      |    | trees nearly to        |      |
|       |      | 1.2m high fence; and                              | which        |                 |      |    | construction           |      |
|       |      | ■ Transplant preparation works                    | should be    |                 |      |    | work are not           |      |
|       |      | shall be carried as soon as possible              | suitable for |                 |      |    | properly fenced.       |      |
|       |      | after commencement of construction.               | healthy      |                 |      |    |                        |      |
|       |      | Rootball and crown pruning shall be               | tree         |                 |      |    | Reinstatement:         |      |
|       |      | carried out over a period of at least 1           | growth.      |                 |      |    | To commence.           |      |
|       |      | month.  |              |                 |      |    |                        |      |
| -     |      |   |              |                 |      |    |                        |      |
| Table | MT 7 | Existing shrub and ground cover                   | All retained | HKJC's          | х    |    | x Construction:        | Nil  |
| 7.31  |      | planting areas that will not be removed           | planting     | Contractor      |      |    | Generally              |      |
|       |      | shall be maintained in good condition             | areas        |                 |      |    | satisfactory.          |      |
|       |      | and enhanced where practical.                     |              |                 |      |    |                        |      |
|       |      |   |              |                 |      |    | Reinstatement:         |      |
|       |      |   |              |                 |      |    | To commence.           | 11   |
|       |      |   |              |                 |      |    |                        |      |
|       | MS 8 | Site formation works at slopes shall be           | Slope        | Event           | х    |    | x Construction:        | Nil  |
|       |      | followed with hydroseeding as soon as             | areas        | Operator        |      |    | Complied.              |      |
|       |      | practical or be covered with shrubs               |              | HKJC's          |      |    |                        |      |
|       |      | and groundcovers.                                 |              | Contractor      |      |    | Reinstatement:         |      |
|       |      |   |              |                 |      |    | To commence            |      |
|       |      |   |              |                 |      |    |                        |      |
|       |      |   |              |                 |      |    |                        |      |
|       |      |   |              |                 |      |    |                        |      |
|       |      |   |              |                 |      | 1  |                        |      |
|       |      |   |              |                 |      |    |                        |      |
|       |      | -   |              |                 |      |    |                        |      |
| Table | MS 9 | Grassing shall be carried out as soon             | General      | Event           | х    |    | Construction:          | Nil. |
| 7.31  |      | as practical after construction of                | Training     | Operator        |      |    | Complied.              |      |
|       |      | footing stratum at one of the General             | Arena        |                 |      |    |                        |      |
|       |      | Training Arenas.                                  |              |                 |      |    |                        |      |
|       |      |   |              |                 |      |    |                        |      |
|       |      |   |              |                 |      |    |                        |      |
| -     |      |   |              |                 | _    | _  |                        |      |

|       |      |  | zan sesting . |            | 1 |   | ^ |                |      |
|-------|------|--|---------------|------------|---|---|---|----------------|------|
| Table | MF 1 | All floodlight units on the floodlight   | Main          | HKJC's     |   | х | х | Operation:     | Nil. |
| 7.31  |      | poles shall be properly aimed at the     | Arena and     | Contractor |   |   |   | Complied.      |      |
|       |      | competition and practice areas of the    | Warm-up       |            |   |   |   |                |      |
|       |      | Main and Warm-up arenas. In this         | Arena         |            |   |   |   | Reinstatement: |      |
|       |      | regards, the central light focus of each |               |            |   |   |   | To commence.   |      |
|       |      | floodlight unit shall always be aimed    |               |            |   |   |   |                |      |
|       |      | on the arena areas and not on any        |               |            |   |   |   |                |      |
|       |      | other adjacent area.                     |               |            |   |   |   |                |      |
|       |      |  |               |            |   |   |   |                |      |
| Table | MF 2 | Each floodlight unit shall have a        | Main          | HKJC's     | x |   |   | Construction:  | Nil. |
| 7.31  |      | built-in anti-glare baffle and visor     | Arena and     | Contractor |   |   |   | Complied.      |      |
|       |      | shield to limit the glare.               | Warm-up       |            |   |   |   |                |      |
|       |      |  | Arena         |            |   |   |   |                |      |
| Table | MF 3 | Operational hours of the floodlights     | Main          | Event      |   | x | х | Operation:     | Nil. |
| 7.31  |      | shall be restricted to competition hours | Arena and     | Operator   |   |   |   | Complied.      |      |
|       |      | only. Floodlights shall be turned off    | Warm-up       |            |   |   |   |                |      |
|       |      | when spectators have left the seating    | Arena         |            |   |   |   | Reinstatement: |      |
|       |      | area.                                    |               |            |   |   |   | To commence.   |      |
|       |      |  |               |            |   |   |   |                |      |
|       |      |  |               |            |   |   |   |                |      |

\* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

\*\* C=Construction, O=Operation R=Reinstatement

Not applicable

# 2. Recommendations and Conclusion

The Contractor shall remove all wild climbers on the transplanted trees areas and remove all dead branches of retained trees.

Appendix G

Log records and details of environmental complaints

## Log Record on Environmental Complaints

| No. | Date of Complaint<br>Received | Description                                      | Investigation Result and Proposed Actions   | Completion<br>Date | Remarks  |
|-----|-------------------------------|--|---|--------------------|--|
| 001 | 28 Aug 2006                   | Discharge of muddy water into<br>Shing Mun River | No evidence had shown the source of the muddy water discharge from subjected site. In fact, there were three main contractors working inside the HKSI area and all share the same discharge outlet. However, contractor had carried out the following measures to prevent any further discharge of muddy water from the subject site areas: | 1 Sept 2006        | EPD inspected the site drainage system on 1 Sept 2006 and was satisfied. |
|     |                               |  | Keep closely checking on the performance of the wastewater treatment system;  |                    |  |
|     |                               |  | <ol> <li>Closely monitoring of the discharge outlet at<br/>Shing Mun River and tracing of the source<br/>origin immediately if muddy water was<br/>observed;</li> </ol>   |                    |  |
|     |                               |  | <ol> <li>Made use of the shallow ground areas on site<br/>to temporary trap stormwater inside the site to<br/>prevent any direct discharge;</li> </ol>  |                    |  |
|     |                               |  | <ol> <li>Construction of temporary drainage channel<br/>and use of water pump to properly divert the<br/>trapped stormwater to the temporary sump<br/>pit;</li> </ol>   |                    |  |
|     |                               |  | <ol> <li>Control pumping of all muddy water collected<br/>from the sump pit to the wastewater treatment<br/>plant within its treatment capacity before<br/>discharging.</li> </ol>  |                    |  |
|     |                               |  |   |                    |  |

| No. | Date of Complaint<br>Received | Description   | Investigation Result and Proposed Actions  | Completion<br>Date | Remarks   |
|-----|-------------------------------|---|--|--------------------|---|
| 002 | 27 Sep 2006                   | Construction dust from construction site at HKSI                            | No direct evidence was found during Contractor's investigation. The Contractor had reviewed the site dust mitigation measures, including more frequent haul road watering and covering the dusty materials.  | 27 Sep 2006        | EPD was replied on<br>28 Sept 2006 by<br>email.   |
| 003 | 8 Nov 2006                    | Construction Noise generated from<br>area at HKSI on 5 Nov 2006<br>(Sunday) | <ol> <li>Rectification action:</li> <li>Introduction of the Permit to Work system for works to be carried out during restricted hours.</li> <li>Consider to apply for a more realistic CNP for the construction works.</li> </ol>  | 12 Nov 2006        | EPD was replied on<br>10 Nov 2007 by<br>email.  |
| 004 | 9 Nov 2006                    | Dust nuisance from construction site of HKSI                                | Rectification action:     Avoid stockpile of dusty materials on site.     Compact the exposed areas when watering on these areas is not effective.   | 9 Nov 2006         | EPD inspected on<br>10 Nov 2006. There<br>was no adverse<br>comment.  |
| 005 | 15 Nov 2006                   | Dump trucks not covering their load were found at the dumping sites         | <ol> <li>Rectification action:</li> <li>Enhancement of the current checking system at vehicular entrance by security personnel.</li> <li>Give warning to subcontractors and establish penalty measures.</li> <li>Give warning to the security company for the site and request them to enhance the checking system for every dump truck leaving the site.</li> </ol> | 17 Nov 2006        | EPD inspected on<br>23 Nov 2006. The<br>rectify actions were<br>introduced and they<br>had no further<br>comment. |
| 006 | 21 Nov 2006                   | Muddy water from construction site at HKSI                                  | Muddy water was observed during Amber rainstorm. Rectification action included installing more water pumps to direct surface runoff.   | 22 Nov 2006        | EPD was replied on 21 Nov 2006 by email.  |
| 007 | 8 Jan 2007                    | Dust and effluent from construction   | Investigation Result:  | 9 Jan 2007         | EPD inspected on 9  |

| No. | Date of Complaint<br>Received | Description   | Investigation Result and Proposed Actions   | Completion<br>Date | Remarks   |
|-----|-------------------------------|---|---|--------------------|---|
|     |                               | site at HKSI  | <ol> <li>Dust and muddy water spread to cycle track during the drilling processes.</li> <li>Rectification action:</li> <li>Clean cycle track regularly</li> <li>Erect screen along the cycle track</li> </ol>   |                    | Jan 2007. They were<br>satisfied with the<br>improvement works.<br>EPD was replied on<br>12 Jan 2007 by<br>email.           |
| 008 | 15 Jan 2007                   | Construction dust from construction site at HKSI                      | Investigation Result:  2. Dust and muddy water spread to cycle track during the drilling processes.  Rectification action:  1. Additional screen was erected and worker was arranged to clean the cycle track regularly.                                | 15 Jan 2007        | EPD believed it was<br>the same complaint<br>as the one on 8 Jan<br>2007. EPD was<br>replied on 15 and 16<br>2007 by email. |
| 009 | 2 Apr 2007                    | Discharge of muddy water to Shing<br>Mun River Channel                | Rectification action:     Installation of additional water pump at the last manhole to direct as much muddy water as possible during rainfall to the on-site treatment facility.  | 3 Apr 2007         | The discharge of muddy water occurred after a heavy rainfall on 2 April 2007. EPD was replied on 3 April 2007 by email.     |
| 010 | 2 Apr 2007                    | Dust and night time construction noise from construction site at HKSI | <ol> <li>Investigation result:</li> <li>No construction activity was scheduled during the concerned period.</li> <li>Rectification action:</li> <li>more frequent haul road watering</li> <li>covering dusty material with tarpaulin sheets.</li> </ol> | 2 Apr 2007         | EPD was replied on<br>3 April 2007 by<br>email.   |

| No. | Date of Complaint<br>Received | Description  | Investigation Result and Proposed Actions  | Completion<br>Date | Remarks   |
|-----|-------------------------------|--|--|--------------------|---|
| 011 | 10 Apr 2007                   | Public holiday construction noise<br>and muddy water in Shing Mun<br>River near the construction site at<br>Yuen Wo Road | <ol> <li>Investigation result:</li> <li>The rainfall on 8 Apr 2007 was 0.3mm, overflowing of site drainage did not occur</li> <li>Only internal finishing works was arranged on 8 Apr 2007, which did not lead to excessive noise</li> <li>The complaint was not substantiated.</li> </ol> | 10 Apr 2007        | EPD inspected on<br>10 April and no<br>further comment.   |
| 012 | 17 Apr 2007                   | Construction dust from construction site at HKSI   | Rectification action:  1. more frequent haul road watering  2. covering dusty material with tarpaulin sheets   | 17 Apr 2007        | EPD was replied on<br>19 and 22 Apr 2007<br>by email.   |
| 013 | 18 Apr 2007                   | Polluted effluent discharged from the construction site at HKSI  | Investigation result:  1. Muddy water was observed after the rainfall on 17 Apr 2007.  Rectification action:  1. More pumps were installed at the last manhole   | 18 Apr 2007        | On site checking with EPD on the same day revealed that muddy water was caused by the tide washing over the river sediment. |
| 014 | 25 Apr 2007                   | Muddy water from construction site at HKSI   | Investigation result:     Muddy water was observed at outfall, but the source of the muddy water could not be traced. The Contractor will keep tracing the source of pollutant.  | 25 Apr 2007        | EPD was replied on<br>27 and 29 Apr 2007<br>by email.   |
| 015 | 9 May 2007                    | No water spraying during granite polishing   | Investigation result: 1. Check cutting processes in all stable areas 2. EPD was replied by email and the complaint was not substantiated   | 9 May 2007         | EPD was replied on 9 May 2007.  |

| No. | Date of Complaint<br>Received | Description   | Investigation Result and Proposed Actions  | Completion<br>Date | Remarks   |
|-----|-------------------------------|---|--|--------------------|---|
| 016 | 23 May 2007                   | Discharge of muddy material to<br>Shing Mun River   | Investigation result:  1. Checking drainage system to prevent any leakage of untreated surface runoff Rectification action:  1. Install more water pumps to direct surface runoff  2. Arrange workers entering the manholes to clear all settled soil  | 31 May 2007        | EPD was replied on<br>31 May 2007   |
| 017 | 31 May 2007                   | Strong light effect from lighting test  | Rectification Action:     Switch off the light within 15 mins after receipt of complaint     Respond to complainant about the rectification action taken     Check the angle of the light to ensure it is not directed to the residential buildings     Self-checking of light at night  | 1 June 2007        | The complainants were informed on 31 May and 1 June of the rectification action taken |
| 018 | 13 June 2007                  | Light nuisance from HKSI after 11:00pm  | Rectification Action:  1. Cancellation of light test on 13 June 2007.  2. The complainant was contacted and agreed to shorten the light test to 10:00pm.  3. All antiglare baffles and visor shields were checked on 14 June to be properly installed.  4. The electricians were reminded on 14 June to aim the flood lights at the main arena and warm up arena before switching on the lights. | 16 June<br>2007    | EPD was replied on 16 June 2007.  |
| 019 | 26 Jun 2007                   | Discharge of muddy water to Shing<br>Mun River from outfall near the site<br>office and wastewater treatment unit | Investigation result:  1. The Hong Kong Observatory record was checked which showed that raining occurred in Shatin during the concerned period.  Rectification Action:  1. Checking of drainage system on 26 June to ensure no leakage of untreated water to Shing Mun River Channel occurred.  2. Checking of water pumps on 26 June to ensure they were well functioned and that              | 27 June<br>2007    | EPD was replied on 27 June 2007.  |

| No. | Date of Complaint<br>Received | Description   | Investigation Result and Proposed Actions  | Completion<br>Date | Remarks                         |
|-----|-------------------------------|---|--|--------------------|---------------------------------|
|     |                               |   | all surface runoff was diverted to the wastewater treatment unit.  3. Checking of wastewater treatment unit on 26 June to ensure that it was well functioned.  |                    |                                 |
| 20  | 29 June 2007                  | Dust and night time construction noise beyond 12:00am                     | Investigation Result:  1. Muddy water absorbed on the cycle track was suspected to lead to the dust complaint.  2. No construction works was arranged beyond 11:00pm. It was estimated the operation of the permanent ventilation system arisen the misunderstanding.  Rectification Result:  1. Covering the exposed slope to prevent soil from washing to cycle track during rain on 1 July.  2. Intercepting the site boundary along cycle track on 3 July to prevent leakage.  3. Clearing up the cycle track on 4 July.   | 4 July 2007        | EPD was replied on 4 July 2007. |
| 21  | 30 June 2007                  | Discharge of muddy materials into Shing Mun River channel and cycle track | Investigation Result:  1. Seeping of minor muddy water to Shing Mun River occurred after heavy rainfall from the outfall near the wastewater treatment unit.  2. Some soil was washed to cycle track due to the removal of site hoarding.  Rectification Result:  1. Checking of water pumps on 30 June 2007 to ensure they functioned well and all surface runoff was diverted to the wastewater treatment unit  2. Checking of wastewater treatment unit on 30 June 2007 to ensure it was well functioned.  3. Covering the exposed slope to prevent soil from washing to cycle track during rain on 1 July. | 4 July 2007        | EPD was replied on 4 July 2007. |

| No. | Date of Complaint Received | Description  | Investigation Result and Proposed Actions   | Completion<br>Date | Remarks                          |
|-----|----------------------------|--|---|--------------------|----------------------------------|
|     |                            |  | <ul><li>4. Intercepting the site boundary along cycle track on 3 July to prevent leakage.</li><li>5. Clearing up the cycle track on 4 July.</li></ul>   |                    |                                  |
| 22  | 27 July 2007               | Light nuisance from HKSI beyond 10:00pm till 11:00pm | Investigation Result:  1. Light testing for all Arenas were completed on 14 July and the whole HKSI venue was locked down on 16 July 2007. There was no light testing carried out sine 15 July 2007 and no more light testing was anticipated to be required.  Rectification Result:  1. Agreed to address to EC via HKJC to notify the public in advance if there is any emergent light testing. | 27 July 2007       | EPD was replied on 27 July 2007. |
