



Emission Control Project at Castle Peak Power Station "B" Units



**Environmental Monitoring
and Audit Monthly Report**

September 2008

Table of Content

| | |
|--|----|
| Executive Summary | 1 |
| 1. Basic Project Information | 5 |
| 1.1 Background | 5 |
| 1.2 Project Organisation..... | 5 |
| 1.3 Construction Activities and Project Programme..... | 5 |
| 1.4 Summary of EM&A Requirements | 6 |
| 2. Environmental Status..... | 11 |
| 2.1 Project Works undertaken during the Reporting Month..... | 11 |
| 2.2 Construction Works to be undertaken in the Coming Month..... | 13 |
| 2.3 Status of Submissions to EPD | 13 |
| 3. Monitoring Results..... | 15 |
| 3.1 Groundwater Monitoring | 15 |
| 3.2 Marine Water Quality Monitoring..... | 15 |
| 3.3 Ecology Monitoring | 16 |
| 4. Implementation Status of EIA Recommendations..... | 18 |
| 4.1 Environmental Mitigation Implementation Schedule..... | 18 |
| 4.2 Implementation status of Event and Action Plan..... | 18 |
| 4.3 Site Environmental Inspection and Audit..... | 18 |
| 4.4 Implementation status of Complaint Handling Procedure..... | 18 |

List of Figures

- Figure 1.1 Location of the EC Project Site
Figure 1.2 EC Project Site General Layout Arrangement
Figure 1.3 Integrated Project Environmental Team

List of Table

- Table 2.1 Key construction works undertaken in the reporting month
Table 2.2 Environmental Permit No. EP-251/2006 - Submissions for Decommissioning/Construction Stage
Table 4.1 Summary of Bi-weekly IEC Site Inspection
Table 4.2 Summary of Weekly ET Site Inspection

List of Photos

- E. 1 Mechanical erection works of Unit B2 FGD Absorber
E. 2 EC Power Distribution Centre (PDC) construction
E. 3 Construction works for the relocated Intermediate Pressure Reducing Station
E. 4 Mechanical erection works for Unit B1 NO_x Reduction Facilities

Appendices

- Appendix A Dolphin Monitoring Sighting Record
Appendix B Construction Phase - Environmental Mitigation Implementation Schedule

Executive Summary

This is the 11th monthly Environmental Monitoring and Audit (EM&A) report for the Emissions Control Project at Castle Peak Power Station 'B' Units (EC Project) prepared by the Environmental Team (ET), with reference to the EPD's Environmental Monitoring and Audit – Guidelines for Development Projects in Hong Kong.

This report presents the implementation status of EM&A requirements in September 2008 as per the Project Environmental Impact Assessment (EIA) Report (EIAO Register No.: AEIAR-102/2006) and Environmental Permit (EP) No. EP-251/2006.

Key Project Works in the reporting month

The key project activities in the reporting month are summarized below:

- Civil Works
 - Mechanical erection works of Unit B2 FGD Absorber. (*Photo E.1*)
 - Site mobilisation of Stack Lining installation works.
 - Pile cap construction for the common Limestone Preparation and Gypsum Dewatering areas, Unit B2 Gas-Gas Heater and the FGD Absorbers of Unit B3 and Unit B4.
 - Bored pile works for Unit B3 Gas-Gas Heater.
 - H-pile construction for the Material Handling System and Limestone Store.
 - Pre-drilling works for Unit B1 and Unit B4 Gas-Gas Heaters.
 - EC Power Distribution Centre (PDC) construction. (*Photo E.2*)
- Material Handling Berth Work
 - Preliminary and site formation works of Material Handling Berth construction.
- Relocation of Existing Facilities
 - Construction works for the relocated Intermediate Pressure Reducing Station (IPRS) (*Photo E.3*)
 - Services diversion, e.g. cables and other station utilities
- NO_x Reduction Facilities Erection
 - Mechanical erection works of Unit B1 NO_x Reduction Facilities (*Photo E.4*)
 - Pre-outage construction works for Unit B4 NO_x Reduction Facilities

Environmental Monitoring

The implementation status of the Project EM&A programmes are summarized below:

- Groundwater monitoring
 - Groundwater monitoring for 2008 is to be conducted on a quarterly basis as per the Groundwater Monitoring Plan (Rev.4), which has been accepted by EPD. The last monitoring was conducted in July 2008

and confirmed that the TPH levels remained well below the relevant Risk-based Remediation Goals (RBRGs) value.

The next sampling is scheduled for October 2008. (*Section 3.1*)

- Marine water quality monitoring
 - Baseline water quality monitoring programme was completed on 21 December 2007 according to the schedule submitted to EPD on 6 November 2007. The Baseline Water Quality Monitoring Report was revised to address EPD's comments on the first submission and re-submitted to EPD on 4 March 2008.
 - According to the EIA report, impact monitoring on marine water quality shall be carried out 3 days a week, at mid-flood and mid-ebb tides, during the dredging works. There was no dredging works conducted during the reporting month and therefore impact monitoring was not required. (*Section 3.2*).
- Ecology monitoring
 - According to the EIA report, visual cetaceans monitoring is required solely during underwater percussive piling works. Underwater percussive piling works for a trial pile were conducted during the reporting month and visual cetaceans monitoring was carried out as per the Environmental Permit. (*Section 3.3*)

Environmental Mitigation Implementation Schedule

Environmental mitigation measures for the construction stage were implemented as per the EIA Report. (*Section 4.1*)

Implementation Status of Event and Action Plan

Dredging works were not yet commenced in the reporting month so impact monitoring for marine water quality was not required and hence the Event and Action Plan was not applicable. (*Section 4.2*)

Site Environmental Inspection

Joint site inspection was conducted by the ET and contractors on a weekly basis, and independent audit was conducted by the Independent Environmental Checker (IEC) on a bi-weekly basis. All required follow-up actions were implemented by the relevant contractors and verified by the Integrated Project Environmental Team in the subsequent site inspections. (*Section 4.3*)

Environmental Complaint and Enquiries

No complaint or enquiries were received in the reporting month. (*Section 4.4*)

Key Project Works in the reporting month



E. 1 Mechanical erection works of Unit B2 FGD Absorber



E. 2 EC Power Distribution Centre (PDC) construction



E. 3 Construction works for the relocated IPRS



E.4 Mechanical erection works of Unit B1 NOx Reduction Facilities

1. Basic Project Information

1.1 Background

The Emissions Control Project at Castle Peak Power Station “B” Units (the Project) involves the installation of additional emissions control facilities to further reduce air emissions from the operation of these units. The emissions control facilities to be installed in the Castle Peak Power Station “B” Units (CPB) include NO_x reduction facilities and Limestone Flue Gas Desulphurisation (LS FGD) for SO₂ reduction. The location of the Site is presented in *Figure 1.1*. An overview of the Project Site general arrangement is presented in *Figure 1.2*.

1.2 Project Organisation

An Integrated Project Environmental Team has been set up to manage the environmental issues associated with the EC Project. The Project Environmental Team comprises the Project Environmental Team Leader (ETL), the Project Regulatory Compliance and Environmental Officer, and the EPCM ^(Note 1) Contractor Environmental Officer. The Project Environmental Team organisation is depicted in *Figure 1.3*.

1.3 Construction Activities and Project Programme

The construction of the Project involves demolition and relocation of certain existing facilities. While the existing generating units will remain in their current locations, some of the auxiliary and common facilities to the south of the generating units at CPB will be demolished or relocated to provide space for the emission control and related facilities. The scope of the Project is as follows:

- Demolition of some existing facilities at CPB including the Fuel Oil Day Tank, Fuel Oil Pump House and Dangerous Goods (DG) Store;
- Relocation or re-routing of existing facilities including Ash and Dust Control Room, Underground Pipeworks, Carbon Dioxide (CO₂) Storage Tank, Liquefied Petroleum Gas (LPG) Storage Tanks, Intermediate Pressure Reduction Station, Oil Interceptors, Oils Sump, Oil Sewer Manholes and Foul Water Pumping Station;
- Provision of Reagent and By-Product Handling and Storage Facilities including limestone silos, limestone slurry tanks, gypsum dewatering and storage facilities;
- Installation of new emission control equipment and facilities for NO_x and SO₂ control;

Note (1) – EPCM stands for Management Contractor of the Engineering, Procurement and Construction (EPC)

- Provision of additional berthing facilities for loading and unloading of the additional reagents and gypsum.

The civil works of the EC Project were commenced on 26 September 2007. These included piling works, foundation works, roads and other civil engineering works and would be executed in a phased manner. Start-up of the retrofitted units are scheduled from end 2009 to 2011.

1.4 Summary of EM&A Requirements

An Environmental Impact Assessment (EIA) for the Project was undertaken and the EIA Report was approved under the *Environmental Impact Assessment Ordinance* (EIAO) (Cap499) on 25 October 2006 (EIAO Register No. AEIAR-102/2006). Environmental Permit (EP) No. EP-251/2006 for the Project was granted on 10 November 2006. Condition 3.2 of the EP requires an EM&A programme to be implemented in accordance with the procedures and requirements set out in the approved EIA Report (EIAO Register No. AEIAR-102/2006).

The EM&A requirements for the EC Project are summarized below:

- Establish baseline water quality levels at designated locations;
- Implement construction impact monitoring programmes for water quality and dolphin monitoring;
- Implement inspection and audit programmes for water quality and dolphin monitoring;
- Liaise with, and provide environmental advice (as requested or when otherwise necessary) to construction site staff on the comprehension and consequences of the environmental monitoring data and exceedances;
- Identify and resolve environmental issues and other functions as they may arise from the works;
- Check and advise the Contractor's overall environmental performance, the implementation of Event and Action Plans (EAPs), and remedial actions taken to mitigate adverse environmental impacts as they may arise from the works;
- Conduct monthly reviews of monitored impact data as the basis for assessing compliance with the defined criteria and to ensure that necessary mitigation measures are identified and implemented, and to undertake additional ad hoc monitoring and auditing as required by special circumstances;
- Evaluate and interpret all environmental monitoring data to provide an early indication should any of the environmental control measures or practices fail to achieve the acceptable standards, and to verify the environmental impacts predicted in the EIA Report;
- Manage and liaise with other individuals or parties concerning other environmental issues deemed to be relevant to the construction process;

- Conduct regular site inspections to assess:
 - the level of the Contractor's general environmental awareness;
 - the Contractor's implementation of the conditions in the EP and the recommendations in the EIA Report;
 - the Contractor's performance as measured by the EM&A programme;
 - the need for specific mitigation measures to be implemented or the continued usage of those previously agreed; and
 - to advise the Site Staff of any identified potential environmental issues.

- Submit Monthly EM&A Reports which summarize environmental monitoring and auditing data, with interpretation illustrating the acceptability or otherwise of any environmental impacts and identification or assessment of the implementation status of agreed mitigation measures.

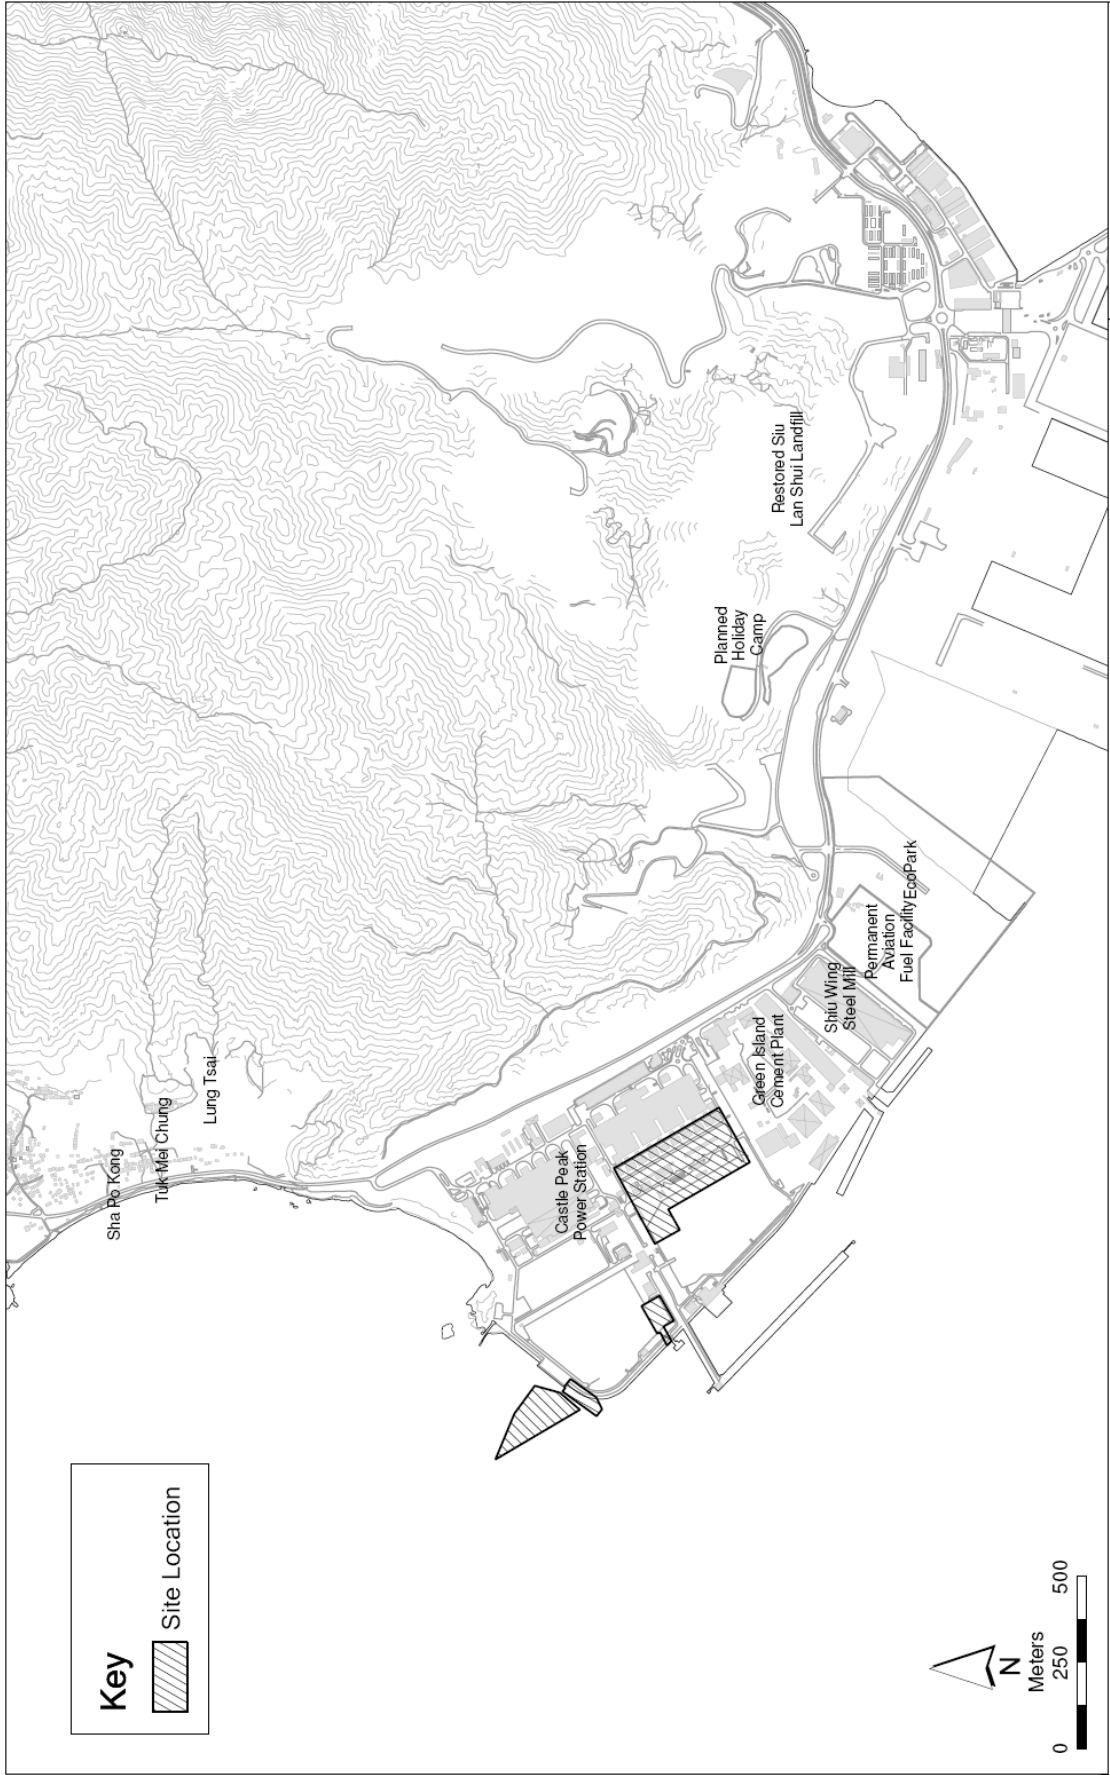


Figure 1.1 Location of the EC Project Site

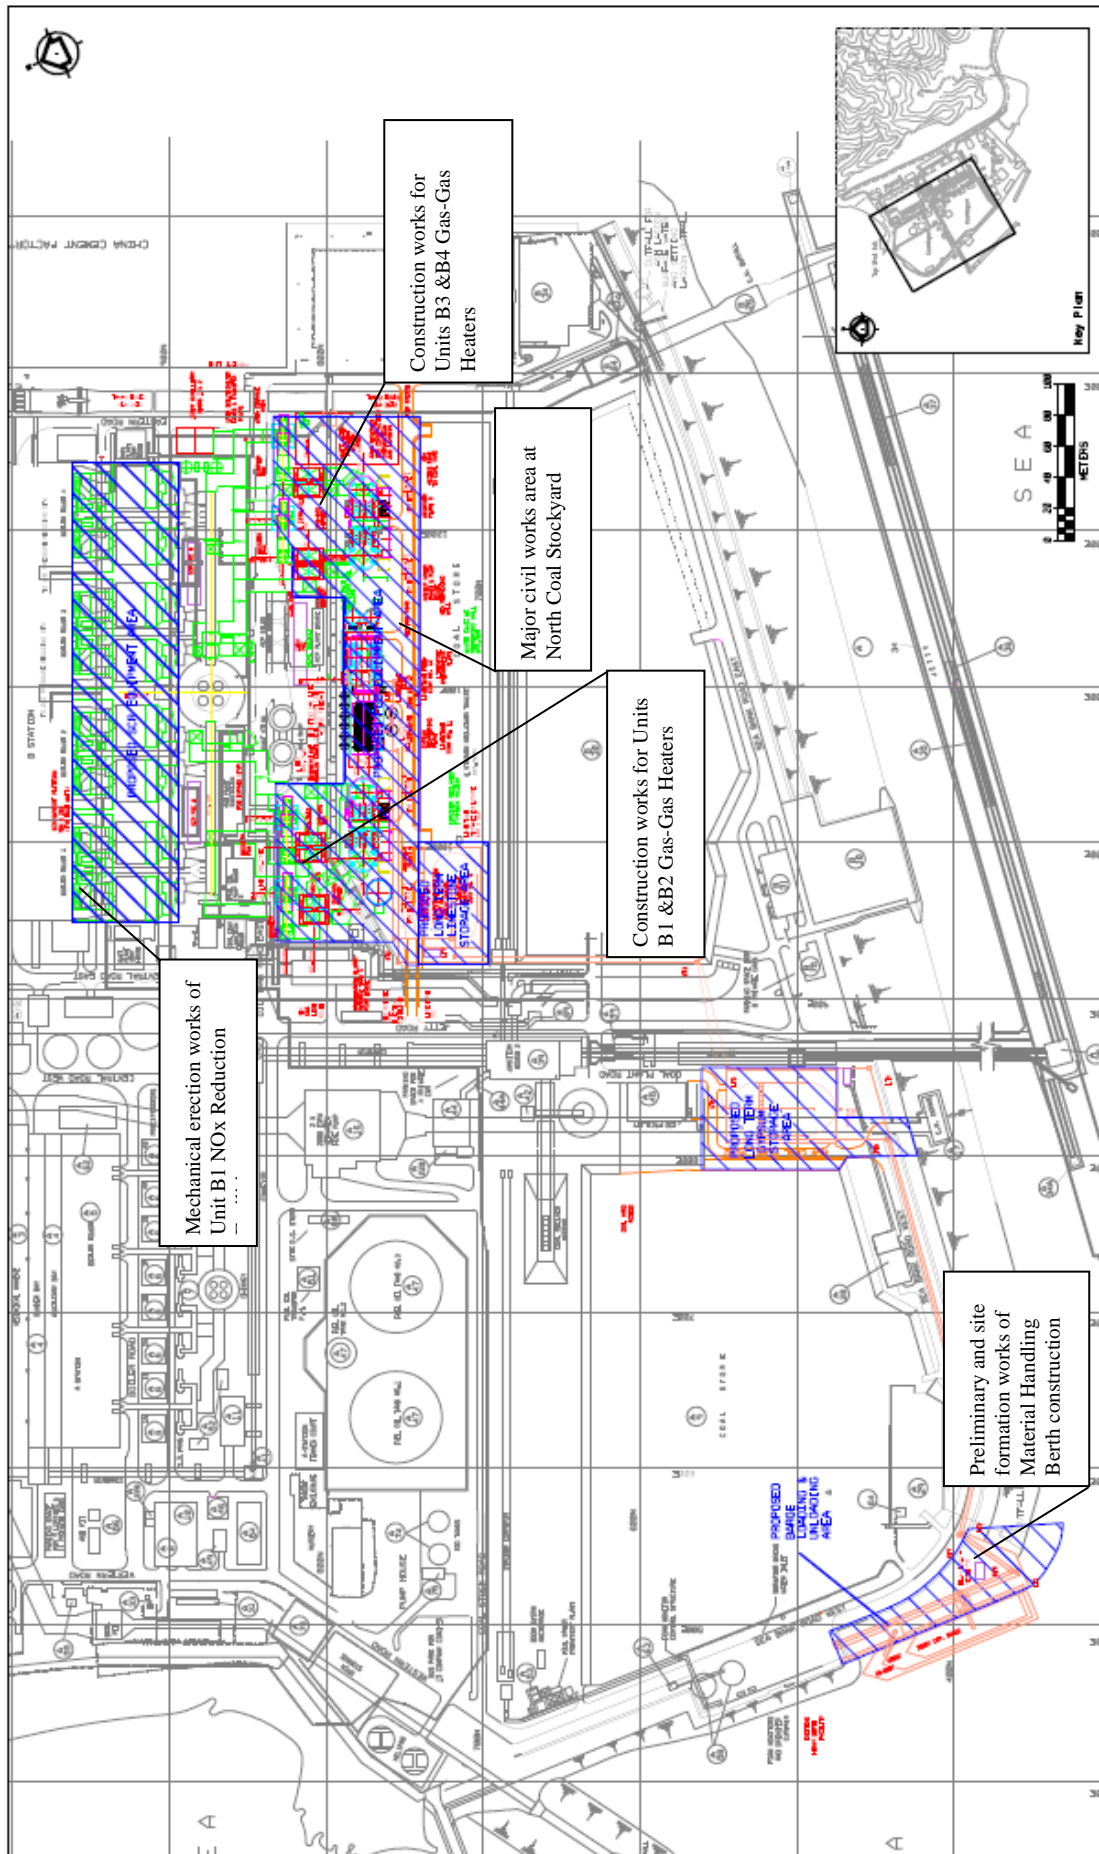


Figure 1.2 EC Project Site General Layout Arrangement

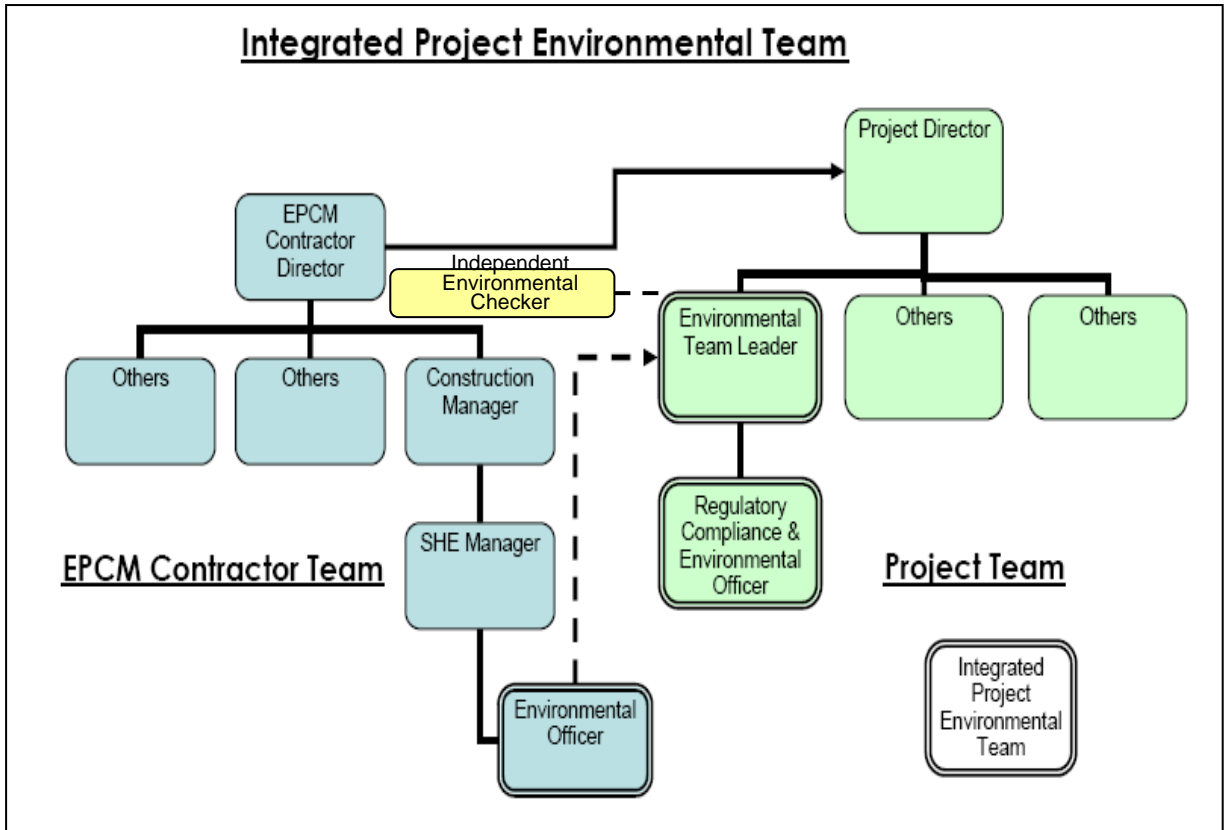


Figure 1.3 Integrated Project Environmental Team

2. Environmental Status

2.1 Project Works undertaken during the Reporting Month

The key site works undertaken in the reporting month and implementation of the required environmental protection measures are summarized in *Table 2.1* below.

Table 2.1 Key construction works undertaken in the reporting month

| | Construction Activities | Environmental Protection Measures |
|-----------------------------------|---|---|
| Civil Works | <ul style="list-style-type: none"> • Mechanical erection works of Unit B2 FGD Absorber. • Site mobilisation of Stack Lining installation works. • Pile cap construction for the common Limestone Preparation and Gypsum Dewatering areas, Unit B2 Gas-Gas Heater and the FGD Absorbers of Unit B3 and Unit B4. • Bored pile works for Unit B3 Gas-Gas Heater. • H-pile construction for the Material Handling System and Limestone Store. • Pre-drilling works for Unit B1 and Unit B4 Gas-Gas Heaters. • EC Power Distribution Centre (PDC) construction. | <ul style="list-style-type: none"> • Dust suppression on access roads; • Temporary stockpiles were either wetted or covered by tarpaulin sheet to prevent dust emission; • Wheel wash facility in place to prevent mud trail by vehicles leaving the project site; • Spillage control measures (e.g. drip tray, spill kit) were implemented; • Proper on-site chemical waste store was provided. |
| Relocation of Existing Facilities | <ul style="list-style-type: none"> • Construction works for the relocated Intermediate Pressure Reducing Station • Services diversion, e.g. cables and other station utilities | <ul style="list-style-type: none"> • Wheel wash facility in place to prevent mud trail by vehicles leaving the project site; • Spillage control measures (e.g. drip tray, spill kit) were implemented; • Dust suppression measures in place; • Proper on-site chemical waste store was provided. |

| | Construction Activities | Environmental Protection Measures |
|------------------------------|---|--|
| Material Handling Berth Work | <ul style="list-style-type: none"> • Preliminary and site formation works of Material Handling Berth construction. | <ul style="list-style-type: none"> • Dust suppression measures in place • Spillage control measures (e.g. drip tray, spill kit) were implemented • Proper on-site chemical waste store was provided |

2.2 Construction Works to be undertaken in the Coming Month

The key site activities in the coming month are summarized below:

- Civil Works
 - Commence Unit B1 Stack Lining installation works.
 - Continue Unit B1 NOx Reduction Facilities.
 - Continue pile cap construction for the FGD Absorbers of Unit B3 and B4.
 - Continue pile construction for the Gas-Gas Heaters, Limestone Store and other areas.
 - Continue construction works for the EC Power Distribution Centre (PDC).
- Relocation of Existing Facilities
 - Continue construction works for the relocated IPRS.
- NOx Reduction Facilities
 - Continue mechanical erection works of Unit B1 NOx Reduction Facilities.
- Flue Gas Desulphurization Absorbers
 - Mechanical erection of the Unit B2 FGD Absorber is underway.

The potential environmental impacts associated with the above construction works include dust emission, construction surface runoff, oil spillage and chemical wastes. Preventive measures have been and will continue to be implemented as per the Environmental Mitigation Implementation Schedule for EC Project Construction Phase.

2.3 Status of Submissions to EPD

The status of submissions to EPD as required under the Environmental Permit No. EP-251/2006 is summarized in *Table 2.2* below.

Table 2.2 Environmental Permit No. EP-251/2006 - Submissions for Decommissioning / Construction Stage

| EP Condition Ref | Submission | Timing for Submission | Target Submission Date | Actual Submission Date |
|--|---|---|-------------------------------|---|
| General Conditions | | | | |
| 1.11 | Commencement Dates of decommissioning and construction of the Project | At least 2 weeks before the commencement of decommissioning and construction respectively | As per schedule | 4/07/07 & 20/08/07 respectively |
| Submission before/after Commencement of Decommissioning/Construction of the Project | | | | |
| 2.3 | Management organisation of the main decommissioning/construction companies and/or any form of JV associated with the Project (including organisation chart, names of responsible persons and their contact details) | At least 1 month after commencement of decommissioning/construction of the Project | As per schedule | 26/10/07 |
| 2.4 | Details of any change to emission reduction process described and assessed in the EIA Report (Register No.: AEIAR - 102/2006) for | At least 3 months before commencement of construction of relevant facilities | If applicable | |
| EM&A Requirements | | | | |
| 3.1 | Groundwater Monitoring Plan | At least 1 month before commencement of construction of the Project | As per schedule | 1st issue - 20/07/07 2nd issue - 5/09/07 3rd issue - 20/11/07 4th issue - 27/02/08 |
| 3.3 | Baseline Water Quality Monitoring Report | At least 1 month before commencement of dredging works | As per schedule | 1st issue - 29/01/08 2nd issue - 4/03/08 |
| 3.4 | Monthly EM&A Report | Within 10 working days at the end of the reporting month | As per schedule | As per schedule |
| 3.5 | Post-Project Monitoring Report for Dredging Works | Within 1 week of completion of the Post-Project Monitoring for the dredging works | As per schedule | |
| Electronic Reporting of EM&A Information | | | | |
| 4.2 | Written notification on the internet address of EM&A website to Director of Environmental | Within 6 weeks after the commencement of construction of the Project | As per schedule | 06/11/07 |

3. Monitoring Results

3.1 Groundwater Monitoring

With respect to the requirement specified in the Environmental Permit No. EP-251/2006, monitoring of the total petroleum hydrocarbon (TPH) in the groundwater within the Project site during construction and operation of the Project is required. A Groundwater Monitoring Plan has been developed to define the groundwater monitoring locations, methodology for groundwater monitoring as well as the monitoring schedule.

Bi-weekly Groundwater Monitoring Programme for the initial period of three months after the commencement of major piling and foundation works was successfully concluded on 25 January 2008. The TPH monitoring results for the initial three-month period consistently remained well below the relevant Risk-based Remediation Goals (RBRGs) values, and therefore the remaining groundwater monitoring for 2008 is to be conducted on a quarterly basis in accordance with the Groundwater Monitoring Plan (Rev 4), which has been accepted by EPD.

The last monitoring was conducted in July 2008 and confirmed that the TPH levels remained well below the relevant Risk-based Remediation Goals (RBRGs) value.

The next sampling is scheduled for October 2008.

3.2 Marine Water Quality Monitoring

With respect to the requirement specified in the Environmental Permit No. EP-251/2006, monitoring of marine water quality during the construction phase is required to evaluate whether any impacts would be posed by the dredging operations on the surrounding waters during the construction period of the dredging works. Baseline monitoring (prior to the dredging works), impact monitoring (during any works related to the dredging works) and post-project monitoring (after completion of the dredging) shall be carried out according to the monitoring locations, monitoring parameters and frequency specified in the EIA Report.

Baseline water quality monitoring programme was completed on 21 December 2007 according to the schedule submitted to EPD on 6 November 2007. The Baseline Water Quality Monitoring Report was revised to address EPD's comments on the first submission and re-submitted to EPD on 4 March 2008.

According to the EIA report, impact monitoring on marine water quality shall be carried out 3 days a week, at mid-flood and mid-ebb tides, during the dredging works. There was no dredging works

conducted during the reporting month and therefore impact monitoring was not required.

3.3 Ecology Monitoring

With respect to the requirement specified in the Environmental Permit No. EP-251/2006, visual cetacean monitoring should be conducted during the underwater percussive piling works to evaluate whether there have been any effects on the animals.

Underwater percussive piling works for a trial pile were conducted during the reporting month and visual cetaceans monitoring was carried out as per the Environmental Permit.

3.3.1 Monitoring Duration and Frequency

Daily visual cetaceans monitoring was conducted whenever there was underwater percussive piling works in the reporting month.

3.3.2 Monitoring Methodology

Dolphin Exclusion Zone

A dolphin exclusion zone was identified within a radius of 500 m from the percussive piling works area. The exclusion zone around the work area was scanned for at least 30 minutes prior to the commencement of piling. If cetaceans were observed in the exclusion zone, underwater percussive piling would be delayed until they had left the area.

Dolphin Observation

The observer was standing at a location on the piling barge that allows for an observation height of 4 to 5 m above water level at the observer's eye level and relatively unobstructed forward visibility. Observation by the observer was conducted by searching with Fujinon 7 x 50 marine binoculars, scanning the area with the naked eye and occasional binocular check. The observer was remained alert at all times during the entire observation period.

Field Record

A sighting record was filled in immediately at the initial sighting with data on the time, position, distance and bearing of the sighting. All other information on sea state, weather conditions (i.e. wind speed according to the Beaufort Scale), as well as notes on dolphin appearance, behaviour, direction of movement, response to boat and any other relevant information were completed at the end of the sighting.

Construction works

When dolphins were spotted within the exclusion zone, construction works would cease and would not resume until the observer confirmed that the zone has been continuously clear of dolphins for a period of 30 minutes (thereby adequately spanning the approximate maximum dive time of the dolphins of 4 minutes). Dolphin sighting position, data on sighting angle, distance to the group, group size and behaviour were recorded.

3.3.4 Monitoring Result

No dolphin was spotted within the exclusion zone during the underwater percussive works in the reporting month. The dolphin monitoring sighting record is given in *Appendix A*.

4. Implementation Status of EIA Recommendations

4.1 Environmental Mitigation Implementation Schedule

Environmental mitigation measures for the construction stage were implemented as per the EIA Report.

An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in *Appendix B*.

4.2 Implementation status of Event and Action Plan

Dredging works has not yet commenced in the reporting month so impact monitoring for marine water quality was not required and hence the Event and Action Plan was not applicable.

4.3 Site Environmental Inspection and Audit

Independent Environmental Checker (IEC) conducted bi-weekly site inspection on the 12th and 26th September 2008 respectively. All the follow-up actions to respond to the IEC observations have been completed by the relevant contractors and verified in the subsequent site inspections by the Integrated Project Environmental Team.

Summary of the IEC site inspections is shown in *Table 4.1*.

Joint site audits were carried out by the Integrated Project Environmental Team (ET) with contractors on a weekly basis to monitor environmental issues at the construction sites to ensure that all mitigation measures were implemented timely and properly. All required mitigation measures were implemented by the relevant contractors and verified in the subsequent site inspections by the Integrated Project Environmental Team.

Summary of the weekly ET site inspections is shown in *Table 4.2*.

4.4 Implementation status of Complaint Handling Procedure

There was no environmental complaint or enquiry received in the reporting month.

Table 4.1 Summary of Bi-weekly IEC Site Inspections

| Date of Inspection | Observations | Follow-up action |
|--------------------|--|---|
| 12/09/2008 | <ul style="list-style-type: none"> - Oil was observed on the ground near the proposed Damper Seal Air Plant to the north of New FGD Road. | <ul style="list-style-type: none"> - The oil was cleaned up by the Contractor immediately. |
| | <ul style="list-style-type: none"> - Drums of waste oil and chemicals near the new Material Handling Berth were not put in designated storage areas. | <ul style="list-style-type: none"> - The identified drums of waste oil and chemicals were removed from the site by the Contractor. |
| | <ul style="list-style-type: none"> - The motors of petro-powered vibrators were placed in the working area near the existing ACP plant without drip trays. | <ul style="list-style-type: none"> - Drip tray was provided for the petro-powered vibrator by the Contractor. |
| | <ul style="list-style-type: none"> - Stop plugs in drip trays near the proposed Limestone Slurry Plant in the northern coal yard were observed to be missing. | <ul style="list-style-type: none"> - Stop plugs were replaced to the identified drip trays by the Contractor. |
| 26/09/2008 | <ul style="list-style-type: none"> - Sediment plumes were observed beyond the silt curtains near the Material Handling Berth area. | <ul style="list-style-type: none"> - The current silt curtains were replaced by new silt curtains made of geotextile fabrics to enclose the working area. - Pre-work checking and continuous monitoring of the silt curtains condition carried out by the Contractor. |
| | <ul style="list-style-type: none"> - Small drums of chemicals were placed on bare ground without drip trays near the proposed Limestone Slurry Plant. | <ul style="list-style-type: none"> - Drip trays were provided for the identified drums of chemicals by the Contractor. |

Table 4.2 Summary of Weekly ET Site Inspection

| Week of Inspection | Observations | Follow-up action |
|-----------------------|--|--|
| 31/08/2008-06/09/2008 | - Damaged chemical waste labels in the chemical waste store to be replaced. | - The identified damaged chemical waste labels were replaced by the Contractor. |
| | - Drain plug was found missing in a drip tray for a mobile diesel generator. | - Drain plug was replaced to the identified drip tray by the Contractor. |
| | - Sandbag to be provided to enclose the gullies near to construction sites. | - Sandbags were provided to enclose the gullies near to construction sites by the Contractor. |
| | - Oily water accumulated in the chemical store to be cleaned up. | - Oily water accumulated in the chemical store was cleaned up by the Contractor. |
| 07/09/2008-13/09/2008 | - Drip tray to be provided for a mobile diesel generator. | - Drip tray was provided to the identified mobile diesel generator by the Contractor. |
| | - Mud trail outside the construction site generated by tracked mobile plant to be cleaned up. | - The mud trail was cleaned up by the Contractor. |
| | - Sand bags to be placed to confine the surface runoff generated from construction activities within the construction site area. | - Sand bags were set up to confine construction surface runoff within the construction site area. |
| 14/09/2008-20/09/2008 | - Construction Noise Permit for piling works to be displayed at the vehicular entrance of the MHB site. | - Construction Noise Permit was displayed at the vehicular entrance of the MHB site by the Contractor. |
| | - Oil residue under a mobile plant to be cleaned up. | - The identified oil residue was removed by the Contractor immediately. |
| 21/09/2008-27/09/2008 | - Temporary stockpiles to be properly covered by tarpaulin. | - The identified stockpile was covered by tarpaulin by the Contractor. |
| | - Sufficient quantity of oil absorbent to be maintained at site for emergency use. | - Sufficient quantity of oil absorbent was maintained at site by the Contractor. |
| | - Oily water on the haul road to be cleaned up. | - The oily water was cleaned up by the Contractor immediately. |

Appendices

Appendix A Dolphin Monitoring Sighting Record

Dolphin Monitoring Summary Log

| Sept 2008 | Underwater piling work carried? (Y/ N) | Dolphin observed? (Y/ N) | Remark |
|------------------|---|---------------------------------|---------------|
| 1 | Y | N | |
| 2 | N | - | |
| 3 | N | - | |
| 4 | N | - | |
| 5 | N | - | |
| 6 | N | - | |
| 7 | N | - | |
| 8 | Y | N | |
| 9 | Y | N | |
| 10 | N | - | |
| 11 | Y | N | |
| 12 | Y | N | |
| 13 | N | - | |
| 14 | N | - | |
| 15 | N | - | |
| 16 | N | - | |
| 17 | N | - | |
| 18 | N | - | |
| 19 | N | - | |
| 20 | N | - | |
| 21 | N | - | |
| 22 | N | - | |
| 23 | N | - | |
| 24 | N | - | |
| 25 | N | - | |
| 26 | N | - | |
| 27 | N | - | |
| 28 | N | - | |
| 29 | N | - | |
| 30 | N | - | |

DOLPHIN / PORPOISE SIGHTING SHEET

Dolphin Observer
觀察員 SC02099 林佛義

Sighting No.
觀察記錄編號 01

HIGH PRIORITY DATA (Record at Initial Piling) 打樁前記錄

Date 日期 1-9-2008 Time 時間 由 10:30 至 12:00

Equipment 儀器 Binoculars 望遠鏡 Compass 指南針

Sighting Distance 觀察距離(metres 米) 5 m 至 500 m

Sighting Angle 觀察角度(°) 5 180° 340°

Sighting Position 觀察位置 Piling Barge E809267.7 N826359.3

Weather Condition 天氣

Sunny 天晴 Rain 雨天 Overcast 陰天

Beaufort 風級 0 1 2 3 4 5 6 7+

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

LOW PRIORITY DATA (Record During or After Piling) 打樁中或後記錄

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

Species Humpback Dolphin 駝背豚 others 其他

品種 Finless Porpoise 江豚

Group Size 群組 Best 很多 _____ High 多 _____ Low 少 _____

CWD Group Composition UC 初生海豚 _____ UJ 無斑點小海豚 _____

群組構成 SJ 斑點小海豚 _____ SS 斑點年青海豚 _____

SA 斑點成年海豚 _____ UA 無斑點成年海豚 _____

FP Group Composition 群組構成 Claves 初生海豚 _____ Adults 成年海豚 _____

BEHAVIOUR 行爲/ COMMENTS 評註

- Feeding 覓食
- Socializing 群聚
- Travelling 游動
- Milling/Resulting 成群兜圈
- Breaching 擊浪
- Spy-hopping 窺探
- Porpoising 躍浪

Other Behaviour 其他行爲 _____

Identified Individual(s) 已識別個體 _____

Other Comments 其他 _____

Observer Signature 海豚觀察員簽名: 林佛義

Piling Supervisor Signature 打樁科文簽名: [Signature]

DOLPHIN / PORPOISE SIGHTING SHEET

Dolphin Observer
觀察員 SC02099 林佛養

Sighting No.
觀察記錄編號 02

HIGH PRIORITY DATA (Record at Initial Piling) 打樁前記錄

Date 日期 1-9-2008 Time 時間 由 14:00 至 19:45
Equipment 儀器 Binoculars 望遠鏡 Compass 指南針
Sighting Distance 觀察距離 (metres 米) 5 m 至 500 m
Sighting Angle 觀察角度 (°) S 180° : N 340°
Sighting Position 觀察位置 Piling Barge E809267.7 N826359.3

Weather Condition 天氣

Sunny 天晴 Rain 雨天 Overcast 陰天
Beaufort 風級 0 1 2 3 4 5 6 7+

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

LOW PRIORITY DATA (Record During or After Piling) 打樁中或後記錄

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

Species Humpback Dolphin 駝背豚 other 其他 _____

品種 Finless Porpoise 江豚

Group Size 群組 Best 很多 _____ High 多 _____ Low 少 _____

CWD Group Composition UC 初生海豚 _____ UJ 無斑點小海豚 _____

群組構成 SJ 斑點小海豚 _____ SS 斑點年青海豚 _____

SA 斑點成年海豚 _____ UA 無斑點成年海豚 _____

FP Group Composition 群組構成 Claves 初生海豚 _____ Adults 成年海豚 _____

BEHAVIOUR 行爲/ COMMENTS 評註

Feeding 覓食 Socializing 群聚 Travelling 游動
 Milling/Resulting 成群兜圈 Breaching 擊浪 Spy-hopping 窺探
 Porpoising 躍浪

Other Behaviour 其他行爲 _____

Identified Individual(s) 已識別個體 _____

Other Comments 其他 _____

Observer Signature 海豚觀察員簽名: 林佛養

Piling Supervisor Signature 打樁科文簽名: KSLONG
林佛養

DOLPHIN / PORPOISE SIGHTING SHEET

Dolphin Observer

觀察員 SC 02099 林佛養

Sighting No.

觀察記錄編號 03

HIGH PRIORITY DATA (Record at Initial Piling) 打樁前記錄

Date 日期 8-9-2008 Time 時間 由 14:30 至 18:55

Equipment 儀器 Binoculars 望遠鏡 Compass 指南針

Sighting Distance 觀察距離 (metres 米) 5 m 至 500 m

Sighting Angle 觀察角度 (°) 180 . 340

Sighting Position 觀察位置 Piling Barge E 80.9267.7 N 82.6359.3

Weather Condition 天氣

Sunny 天晴 Rain 雨天 Overcast 陰天

Beaufort 風級 0 1 2 3 4 5 6 7+

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

LOW PRIORITY DATA (Record During or After Piling) 打樁中或後記錄

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

Species Humpback Dolphin 駝背豚

Others 其它 _____

品種 Finless Porpoise 江豚

Group Size 群組 Best 很多 _____ High 多 _____ Low 少 _____

CWD Group Composition UC 初生海豚 _____ UJ 無斑點小海豚 _____

群組構成 SJ 斑點小海豚 _____ SS 斑點年青海豚 _____

SA 斑點成年海豚 _____ UA 無斑點成年海豚 _____

FP Group Composition 群組構成 Claves 初生海豚 _____ Adults 成年海豚 _____

BEHAVIOUR 行爲 / COMMENTS 評註

Feeding 覓食 Socializing 群聚 Travelling 游動

Milling/Resulting 成群兜圈 Breaching 擊浪 Spy-hopping 窺探

Porpoising 躍浪

Other Behaviour 其他行爲 _____

Identified Individual(s) 已識別個體 _____

Other Comments 其他 _____

Observer Signature 海豚觀察員簽名: 林佛養

Piling Supervisor Signature 打樁科文簽名: 盧志輝

DOLPHIN / PORPOISE SIGHTING SHEET

Dolphin Observer
觀察員 SC02099 林佛善

Sighting No.
觀察記錄編號 04

HIGH PRIORITY DATA (Record at Initial Piling) 打樁前記錄

Date 日期 9-9-2008 Time 時間 由 10:00 至 14:00

Equipment 儀器 Binoculars 望遠鏡 Compass 指南針

Sighting Distance 觀察距離(metres 米) 5 m 至 500 m

Sighting Angle 觀察角度(°) 180 340

Sighting Position 觀察位置 Piling Barge E809267.7 N826359.3

Weather Condition 天氣

Sunny 天晴 Rain 雨天 Overcast 陰天

Beaufort 風級 0 1 2 3 4 5 6 7+

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

LOW PRIORITY DATA (Record During or After Piling) 打樁中或後記錄

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

Species Humpback Dolphin 駝背豚 other 其它 _____

品種 Finless Porpoise 江豚

Group Size 群組 Best 很多 _____ High 多 _____ Low 少 _____

CWD Group Composition UC 初生海豚 _____ UJ 無斑點小海豚 _____

群組構成 SJ 斑點小海豚 _____ SS 斑點年青海豚 _____

SA 斑點成年海豚 _____ UA 無斑點成年海豚 _____

FP Group Composition 群組構成 Claves 初生海豚 _____ Adults 成年海豚 _____

BEHAVIOUR 行爲/ COMMENTS 評註

Feeding 覓食 Socializing 群聚 Travelling 游動

Milling/Resulting 成群兜圈 Breaching 擊浪 Spy-hopping 窺探

Porpoising 躍浪

Other Behaviour 其他行爲 _____

Identified Individual(s) 已識別個體 _____

Other Comments 其他 _____

Observer Signature 海豚觀察員簽名: 林佛善

Piling Supervisor Signature 打樁科文簽名: [Signature]

DOLPHIN / PORPOISE SIGHTING SHEET

Dolphin Observer

觀察員 SC62099 林偉義

Sighting No.

觀察記錄編號 85

HIGH PRIORITY DATA (Record at Initial Piling) 打樁前記錄

Date 日期 11-9-08 Time 時間 由 13:30 至 17:00

Equipment 儀器 Binoculars 望遠鏡 Compass 指南針

Sighting Distance 觀察距離(metres 米) 5 m 至 500 m

Sighting Angle 觀察角度(°) 190 340

Sighting Position 觀察位置 Piling Barge E 809267.7 N 826359.3

Weather Condition 天氣

Sunny 天晴 Rain 雨天 Overcast 陰天

Beaufort 風級 0 1 2 3 4 5 6 7+

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

LOW PRIORITY DATA (Record During or After Piling) 打樁中或後記錄

Dolphin Found 海豚行蹤 Yes 有 No 沒有

Percussive Piling interruption Time 停工時間: 由 _____ 至 _____

Survey Area 出沒地點 _____

Species Humpback Dolphin 駝背豚 other 其它 _____

品種 Finless Porpoise 江豚

Group Size 群組 Best 很多 _____ High 多 _____ Low 少 _____

CWD Group Composition UC 初生海豚 _____ UJ 無斑點小海豚 _____

群組構成 SJ 斑點小海豚 _____ SS 斑點年青海豚 _____

SA 斑點成年海豚 _____ UA 無斑點成年海豚 _____

FP Group Composition 群組構成 Claves 初生海豚 _____ Adults 成年海豚 _____

BEHAVIOUR 行爲/ COMMENTS 評註

Feeding 覓食 Socializing 群聚 Travelling 游動
 Milling/Resulting 成群兜圈 Breaching 擊浪 Spy-hopping 窺探
 Porpoising 躍浪

Other Behaviour 其他行爲 _____

Identified Individual(s) 已識別個體 _____

Other Comments 其他 _____

Observer Signature 海豚觀察員簽名: 林偉義

Piling Supervisor Signature 打樁科交簽名: [Signature]

DOLPHIN / PORPOISE SIGHTING SHEET

Dolphin Observer
觀察員 SL02099 林佛善

Sighting No.
觀察記錄編號 06

HIGH PRIORITY DATA (Record at Initial Piling) 打樁前記錄

Date 日期 12-9-2008 Time 時間 由 09:00 至 12:30
 Equipment 儀器 Binoculars 望遠鏡 Compass 指南針
 Sighting Distance 觀察距離 (metres 米) 5 m 至 500 m
 Sighting Angle 觀察角度 (°) 180 . 34.0 .
 Sighting Position 觀察位置 Piling Barge E 809267.7 N 826359.3

Weather Condition 天氣

Sunny 天晴 Rain 雨天 Overcast 陰天
 Beaufort 風級 0 1 2 3 4 5 6 7+

Dolphin Found 海豚行蹤 Yes 有 No 沒有
 Percussive Piling interruption Time 停工時間: 由 _____ 至 _____
 Survey Area 出沒地點 _____

LOW PRIORITY DATA (Record During or After Piling) 打樁中或後記錄

Dolphin Found 海豚行蹤 Yes 有 No 沒有
 Percussive Piling interruption Time 停工時間: 由 _____ 至 _____
 Survey Area 出沒地點 _____
 Species 品種 Humpback Dolphin 駝背豚 others 其他 _____
 Finless Porpoise 江豚
 Group Size 群組 Best 很多 _____ High 多 _____ Low 少 _____
 CWD Group Composition UC 初生海豚 _____ UJ 無斑點小海豚 _____
 群組構成 SJ 斑點小海豚 _____ SS 斑點年青海豚 _____
 SA 斑點成年海豚 _____ UA 無斑點成年海豚 _____
 FP Group Composition 群組構成 Claves 初生海豚 _____ Adults 成年海豚 _____

BEHAVIOUR 行爲/ COMMENTS 評註

Feeding 覓食 Socializing 群聚 Travelling 游動
 Milling/Resulting 成群兜圈 Breaching 擊浪 Spy-hopping 窺探
 Porpoising 躍浪

Other Behaviour 其他行爲 _____
 Identified Individual(s) 已識別個體 _____
 Other Comments 其他 _____

Observer Signature 海豚觀察員簽名: 林佛善

Piling Supervisor Signature 打樁科文簽名: 林

Appendix B Construction Phase - Environmental Mitigation Implementation Schedule

Legends:

C - Complied

NC - Not complied

N/A - Not Applicable

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|----------------------|--|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| <i>Air Quality</i> | | | | | | |
| EIA S3.6.1 | <ul style="list-style-type: none"> The area at which demolition work takes place should be sprayed with water prior to, during and immediately after the demolition activities so as to maintain the entire surface wet | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S3.6.1 | <ul style="list-style-type: none"> Dust screens or sheeting should be provided to enclose the structure to be demolished to a height of at least 1 m higher than the highest level of the structure; | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S3.6.1 | <ul style="list-style-type: none"> Any dusty materials should be wetted with water to avoid any fugitive dust emission; | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S3.6.1 | <ul style="list-style-type: none"> All temporary stockpiles should be wetted or covered by tarpaulin sheet to prevent fugitive emissions; | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S3.6.1 | <ul style="list-style-type: none"> All the dusty areas and roads should be wetted with water; | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S3.6.1 | <ul style="list-style-type: none"> All the dusty materials transported by lorries should be covered entirely by impervious sheet to avoid any leakage; and | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S3.6.1 | <ul style="list-style-type: none"> The falling height of fill materials should be controlled. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| <i>Water Quality</i> | | | | | | |
| EP Con 2.14, EIA | <ul style="list-style-type: none"> Silt curtains should be deployed around the closed grab dredger to contain suspended solids within the construction site during dredging. | Within the construction site/Throughout the | Contractor | | ✓ | N/A |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|---------------------------------|--|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| S5.8.1 | | construction period | | | | |
| EP Cons 2.13 & 2.15, EIA S5.8.1 | <ul style="list-style-type: none"> A daily dredging rate of a closed grab dredger (with a minimum grab size of 8 m³) should be less than 5,200 m³ day⁻¹, with reference to the maximum rate for dredging, which was derived in the EIA. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EP Con 2.16, EIA S5.8.1 | <ul style="list-style-type: none"> Barges or hoppers should have tight fitting seals to their bottom openings to prevent leakage of material. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EP Con 2.9 | <ul style="list-style-type: none"> Any groundwater arising from the decommissioning and construction of the Project shall be collected and recharged back to the site of the Project. No groundwater shall be used for any industrial or domestic purposes. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EP Con 2.10 | <ul style="list-style-type: none"> All wastewater or effluent arising from the stockpiling, transportation and treatment of the excavated contaminated materials shall be properly collected and treated. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EP Con 2.11 | <ul style="list-style-type: none"> Surface run-off from the construction site shall be directed into sand/silt removal facilities such as sand/silt traps and sediment basins before discharge. The sand/silt removal facilities shall be adequately designed and properly operated and maintained. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EP Con 2.12, EIA S5.8.2 | <ul style="list-style-type: none"> All exposed earth areas should be completed as soon as possible after earthworks have been completed, or alternatively, within 14 days of the cessation of earthworks, where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or by other means. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.1 | <ul style="list-style-type: none"> Mechanical grabs should be designed and maintained to avoid spillage and should seal tightly while being lifted. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EIA S5.8.1 | <ul style="list-style-type: none"> Loading of barges or hoppers should be controlled to prevent splashing of dredged material to the surrounding water. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EIA | <ul style="list-style-type: none"> Barges or hoppers should not be filled to a level which will cause | Within the construction | Contractor | | ✓ | N/A |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|------------|--|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| S5.8.1 | overflow of materials or pollution of water during loading or transportation. | site/Throughout the construction period | | | | |
| EIA S5.8.1 | <ul style="list-style-type: none"> Excess material should be cleaned from the decks and exposed fittings of barges or hoppers before the vessel is moved. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EIA S5.8.1 | <ul style="list-style-type: none"> Adequate freeboard should be maintained on barges to reduce the likelihood of decks being washed by wave action. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EIA S5.8.1 | <ul style="list-style-type: none"> All vessels should be sized such that adequate clearance is maintained between vessels and the seabed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EIA S5.8.1 | <ul style="list-style-type: none"> The works should not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and adjacent to the works site. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EIA S5.8.2 | <ul style="list-style-type: none"> At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed and internal drainage works and erosion and sedimentation control facilities implemented. Channels, earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of efficient silt removal facilities should be based on the guidelines in <i>Appendix A1 of ProPECC PN 1/94</i>. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> All the surface runoff or extracted ground water contaminated by silt and suspended solids should be collected by the on-site drainage system and diverted through the silt traps prior to discharge into storm drain. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|------------|--|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA S5.8.2 | <ul style="list-style-type: none"> Measures should be taken to reduce the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50 m³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in <i>Appendix A2 of ProPECC PN 1/94</i>. Particular attention should be paid to the control of silty surface runoff during storm events, especially for areas located near steep slopes. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> Oil interceptors should be provided in the drainage system and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages. The interceptor should have a bypass to prevent flushing during periods of heavy rain. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| EIA S5.8.2 | <ul style="list-style-type: none"> All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge should be adequately designed for the controlled release of storm flows. All sediment traps should be regularly cleaned and maintained. The temporary diverted drainage should be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|-------------------------|--|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA S5.8.2 | <ul style="list-style-type: none"> Sewage from toilets should be collected by a licensed waste collector. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> Vehicle and plant servicing areas, vehicle wash bays and lubrication bays should, as far as possible, be located within roofed areas. The drainage in these covered areas should be connected to foul sewers via a petrol interceptor. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> Oil leakage or spillage should be contained and cleaned up immediately. Waste oil should be collected and stored for recycling or disposal, in accordance with the <i>Waste Disposal Ordinance</i>. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> Waste streams classifiable as chemical wastes should be properly stored, collected and treated for compliance with <i>Waste Disposal Ordinance</i> or <i>Disposal (Chemical Waste) (General) Regulation</i> requirements. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> The Contractors should prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S5.8.2 | <ul style="list-style-type: none"> Surface run-off from bunded areas should pass through oil/grease traps prior to discharge to the stormwater system. | Within the construction site/Throughout the construction period | Contractor | | ✓ | N/A |
| <i>Waste Management</i> | | | | | | |
| EP Con 2.19 | No wastes, spoil or excavated materials or materials alike arising from the demolition and/or decommissioning and construction works of the Project shall be dumped in any environmentally sensitive areas, including but not limited to Sites of Special Scientific Interest, coastal protection areas, conservation areas and agricultural land. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|------------|--|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA S6.6.1 | Dredged sediments should be disposed of only at designated disposal sites allocated by the Marine Fill Committee (MFC) based on the findings of further sediment quality tests. A dumping licence should also be obtained from EPD prior to the commencement of the dredging works. | Within designated disposal site/prior to commencement of the dredging works | Contractor | | ✓ | N/A |
| EIA S6.6.1 | Regardless of the disposal method and site, the Contractor should: <ul style="list-style-type: none"> • Dredge the sediments using closed grabs; • Use split barges of not less than 750 m³ capacity when transporting the sediment to the disposal site; • Regularly maintain the barge hoppers to ensure that they are capable of rapid opening and discharge at the designated disposal site; and • Monitor the barge load against loss of materials during transportation. | Within the dredging area /Throughout the dredging works period | Contractor | | ✓ | N/A |
| EIA S6.6.3 | The contractor should open a billing account with EPD in accordance with the <i>Waste Disposal (Charges for Disposal of Construction Waste) Regulation</i> for the payment of disposal charges. Every waste load transferred to government waste disposal facilities such as public fill, sorting facilities, landfills or transfer station would required a valid “chit” which contain the information of the account holder to facilitate waste transaction recording and billing to the waste producer. A trip-ticket system should also be established in accordance with <i>Works Bureau Technical Circular No. 21/2002</i> to monitor the disposal of solid wastes at transfer station/landfills, and to control fly-tipping. The billing “chit” and trip-ticket system should be included as one of the contractual requirements and implemented by the contractor. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S6.6.3 | A recording system for the amount of waste generated, recycled and disposed of (including the disposal sites) should be established during the construction stage. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|---------------|---|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA S6.6.3 | <p><i>Measures for the Reduction of C&DM Generation during Planning and Design Stages</i></p> <p>The various waste management options can be categorized in terms of preference from an environmental viewpoint. The options considered to be more preferable have the least impacts and are more sustainable in the long term. Hence, the waste management hierarchy is as follows:</p> <ul style="list-style-type: none"> • Avoidance and minimization, that is, reduction of waste generation through changing or improving practices and design; • Reuse of materials, thus avoiding disposal (generally with only limited reprocessing); • Recovery and recycling, thus avoiding disposal (although reprocessing may be required); and • Treatment and disposal, according to relevant law, regulations, guidelines and good practice. <p>This hierarchy should be used to evaluate the waste management options, thus allowing maximum waste reduction and reduced disposal costs. Records of quantities of wastes generated, recycled and disposed (locations) should be kept.</p> | Within the construction site/Throughout the construction period | Contractor | ✓ | | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|---------------|--|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA S6.6.3 | <p><i>Measures for the Reduction of C&DM Generation during Construction</i></p> <ul style="list-style-type: none"> • C&D materials will be reused as far as possible within the Project. Public fill and construction waste should be segregated and stored in different containers or skips to facilitate reuse or recycling of materials and their proper disposal of construction waste. Specific areas of the work site should be designated for such segregation and temporary storage if immediate use is not practicable. • The construction waste should be collected by Contractor and transported to landfills for disposal. • The use of wooden hoardings should not be allowed. An alternative material, which can be reused or recycled, for example, metal (aluminium, alloy, etc) should be used. • To reduce the potential dust impact, C&D materials should be wetted as quickly as possible during excavation works. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S6.6.4 | <p>Containers used for storage of chemical wastes should:</p> <ul style="list-style-type: none"> • be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; • have a capacity of less than 450 L unless the specifications have been approved by the EPD; and • display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2 of the Regulations</i> | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|------------|---|---|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA S6.6.4 | The storage area for chemical wastes should: <ul style="list-style-type: none"> • be clearly labelled and used solely for the storage of chemical waste; • be enclosed on at least 3 sides; • have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; • have adequate ventilation; • be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and • be arranged so that incompatible materials are appropriately separated. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S6.6.4 | Disposal of chemical waste should be: <ul style="list-style-type: none"> • via a licensed waste collector; and • to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Facility which also offers a chemical waste collection service and can supply the necessary storage containers | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S6.6.5 | The sewage sludge from the portable toilet should be collected by a reputable collector on a regular basic. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S6.6.6 | General refuse should be stored in enclosed bins or compaction units separately from construction and chemical wastes. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S6.6.6 | General refuse should be removed from the site, separately from construction and chemical wastes, on a daily basis to minimise odour, pest and litter impacts. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S6.6.6 | Burning of refuse on construction site is prohibited by law. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|---------------------------|--|--|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA S6.6.6 | Aluminium cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. As such, separate, labelled bins for their deposit should be provided if feasible. Materials recovered will be re-used on site or sold for recycling. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| EIA S6.6.7 | Training should be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling at the beginning of the Contract. | Within the construction site/Throughout the construction period | Contractor | | ✓ | C |
| <i>Land Contamination</i> | | | | | | |
| EP Con 2.5 | The oil tanks shall be properly cleaned before their demolition. All wastes and effluent arising from the cleaning of the oil tanks shall be properly collected, stored, treated and disposed of. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EP Con 2.6 | No contaminated soil arising from the demolition and/or decommissioning works shall be stockpiled, treated or disposed of outside the Castle Peak Power Station. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EP Con 2.7 | The excavated soil arising from the demolition and/or decommissioning works shall be properly contained in container(s) during storage and transportation to avoid any discharge or leakage. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EP Con 2.8 | The contaminated soil arising from the demolition and/or decommissioning works shall be decontaminated within the Castle Peak Power Station in accordance with the Land Contamination Remediation Action Plan contained in the EIA report (Register No. AEIAR-102/2006). Bio-remediation methods shall be used to remedy the petroleum hydrocarbon contamination in the excavated materials. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | Potentially contaminated soil should be treated in accordance with the remediation actions specified in the Remediation Action Plan (RAP) of this EIA Report and the treated soil should be reused within the Project Site as far as possible. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | The temporary stockpile of excavated potentially contaminated materials should be contained in a container covered by HDPE sheet on top | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | Bioremediation by applying nutrient to the soil should be employed for the on-site treatment of excavated materials potentially contaminated by TPH. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|-------------------------|--|--|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA Annex E | If disposal of the treated excavated soil to the public fill bank is required, vehicles containing any excavated materials should be suitably covered to limit potential dust emissions or wastewater run-off, and truck bodies and tailgates will be sealed to minimise the risk of a discharge during transportation or during wet conditions. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | N/A |
| EIA Annex E | Records of the quantities of soil generated for off-site disposal will be maintained. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EP Con 2.9, EIA Annex E | As groundwater is not used for either domestic or industrial purposes at the site or in the adjacent areas, remediation of groundwater is not considered to be necessary for the Project to proceed. If groundwater is encountered during the construction of foundations, the groundwater abstracted or collected will be recharged back to the site. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | The FODT and the oil separator serving it should be cleaned prior to demolition. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | Oily water and sludge collected from the cleaning should be treated at the on-site wastewater treatment facility. Oily water and sludge collected from the cleaning should be collected and disposed of as chemical waste at Government chemical waste treatment facility. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | Only licensed waste contractors should be used to collect and transport any chemical waste. The necessary waste disposal permits will be obtained, as required, from the appropriate authorities, in accordance with the <i>Waste Disposal Ordinance (Cap 354)</i> and <i>Waste Disposal (Chemical Waste) (General) Regulation (Cap 354C)</i> , as required. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | Prior to commence any remediation work, a health and safety risk assessment should be performed for the remediation work to identify potential work related hazards and prepare appropriate control measures. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | Appropriate Personal Protective Equipment (PPE) such as safety hat, chemical protective gloves, masks (for both dust and vapour), eye goggles, protective clothing and protective footwear should be provided to staff who would be involved in the tank cleaning and contaminated area (FODT and TP3) remediation works. No works should be allowed without the suitable PPE. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|-----------------------------------|--|--|----------------------|----------------------|--------------|--|
| | | | | Design | Construction | |
| EIA Annex E | The workers should inspect and check their PPE before, during and after use. In cases where any of the PPE is impaired, the workers should stop work immediately and inform their supervisor. The workers should not be allowed to re-start their work until the impaired PPE is replaced. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | The workers should always maintain basic hygiene standard (e.g. hand wash before leaving the contaminated work area). The workers should also be responsible for cleaning and storing their own PPE in a secure place before leaving the site. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | Eating, drinking and smoking should be strictly prohibited within the contaminated site area. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | The designated site management representatives must be informed if any workers feel uncomfortable physically or mentally during the remediation works. All workers should leave the work areas and the work should be temporarily suspended until the reason for the uncomfortable feeling has been identified. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | The works should be stopped or discontinued when Typhoon Signal No. 3 or Rainstorm Warning signals are hoisted. All stockpile materials (if any) should be covered immediately by tarpaulin or other similar protective and waterproof materials. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| EIA Annex E | Bulk earth-moving excavator equipment should be used to minimise construction workers' potential contact with contaminated materials. | Within the contaminated area /Throughout the construction period | Contractor | | ✓ | C |
| <i>Ecological – Marine Mammal</i> | | | | | | |
| EP Con 2.17, EIA S8.9 | To limit potential impacts to cetaceans from underwater percussive piling, the following steps should be taken: <ul style="list-style-type: none"> • Only hydraulic hammers should be used; • An exclusion zone of 500 m radius should be scanned around the work area for at least 30 minutes prior to the start of piling. If cetaceans are observed in the exclusion zone, piling should be delayed until they have left the area; and, • Acoustic decoupling of noisy equipment on work barges should be undertaken. These techniques include the use of a soft sling to retain | Within the dredging area /Throughout the construction period | Contractor | | ✓ | C |

| Ref. | Environmental Protection Measures | Location/Duration of Measures/Timing of Completion of Measures | Implementation Agent | Implementation Stage | | Implementation Status during the reporting month |
|-------------|--|--|--|----------------------|--------------|--|
| | | | | Design | Construction | |
| | the pile driving hammer, rubber tyred air compressor for bubble jacket/curtain, rubber pads on barge leaders and guides, and an air curtain around the pile barge. | | | | | |
| EP Con 2.18 | To minimize potential construction and operation impacts on dolphins and porpoises, no dumping of rubbish, food, oil, or chemicals from the marine vessels shall be allowed. | Within the dredging area /Throughout the construction period | Contractor | | ✓ | C |
| EIA S8.9 | <p>The following recommendations should be considered to minimize potential construction impacts on dolphins and porpoises.</p> <ul style="list-style-type: none"> • All vessel operators working on the Project construction should be given a briefing, alerting them to the possible presence of dolphins in the area, and the guidelines for safe vessel operation in the presence of cetaceans. If high speed vessels are used, they should be required to slow to 10 knots when passing through a high density dolphin area (west Lantau, Sha Chau and Lung Kwu Chau); • The vessel operators should be required to use predefined and regular routes, as these will become known to dolphins using these waters; • The vessel operators should be required to control and manage all effluent from vessels; • A policy of no dumping of rubbish, food, oil, or chemicals should be strictly enforced. This should also be covered in the contractor briefings; • Every attempt should be made to minimize the effects of construction of the Project on the water quality of the area; | Within the marine works area /Throughout the construction period of the additional berthing facility | Contractor / CLP Power (as CAPCO operator) | | ✓ | C |
| S9.3.5 | The new structures associated with the Project, including those of the additional conveyor systems, should be painted in a colour scheme that complements the surrounding industrial setting of the existing CPPS. | New structures associated with the Project | Contractor | | ✓ | N/A |
