



Lam Geotechnics Limited

Contract No. HK/2011/07
Wanchai Development Phase II and Central Wanchai Bypass
Sampling, Field Measurement and testing Works (Stage 2)
Quarterly EM&A Report (March 2015 - May 2015)

CONTRACT NO: HK/2011/07

**WANCHAI DEVELOPMENT PHASE II AND CENTRAL
WANCHAI BYPASS
SAMPLING, FIELD MEASUREMENT AND TESTING WORK
(STAGE 2)**

**ENVIRONMENTAL PERMIT NO. EP-356/2009,
FURTHER ENVIRONMENTAL PERMIT NOS. FEP-02/356/2009,
FEP-03/356/2009, FEP-04/356/2009
FEP-06/356/2009 AND FEP-07/356/2009**

**QUARTERLY ENVIRONMENTAL MONITORING
AND AUDIT REPORT**

- MARCH 2015 TO MAY 2015 -

CLIENTS:

**Civil Engineering and Development
Department**

and

Highways Department

PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point
181-185 Gloucester Road,
Wanchai, H.K.

Telephone: (852) 2882-3939
Facsimile: (852) 2882-3331
E-mail: info@lamenviro.com
Website: <http://www.lamenviro.com>

CHECKED BY:

Raymond Dai
Environmental Team Leader

DATE:

25 June 2015

Ref.: AACWBIECEM00_0_6829L.15

29 June 2015

By Post and Fax (2691 2649)

AECOM Asia Company Limited
Engineer's Representative's Office
25 Hung Hing Road,
Causeway Bay,
Hong Kong

Attention: Mr. Peter Poon

Dear Sir,

Re: Wan Chai Development Phase II and Central-Wan Chai Bypass
Quarterly EM&A Report (March 2015 to May 2015) for
EP-356/2009, FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009 and FEP-
07/356/2009

Reference is made to the Environmental Team's submission of the captioned Quarterly Environmental Monitoring and Audit (EM&A) Report for March 2015 to May 2015 received by e-mail on 25 June 2015.

Please be informed that we have no adverse comment on the captioned submission and thereby write to verify the captioned submission.

Thank you very much for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



David Yeung
Independent Environmental Checker

c.c.	HyD	Mr. Bond Chow	by fax: 2714 5289
	CEDD	Mr. Jason Cheung	by fax: 2577 5040
	AECOM	Mr. Francis Leong / Mr. Stephen Lai	by fax: 2691 2649
	AECOM	Mr. Conrad Ng	by fax: 2691 2649
	Lam	Mr. Raymond Dai	by fax: 2882 3331

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00_0_6829L.15.doc

TABLE OF CONTENTS

EXECUTIVE SUMMARY	4
1. INTRODUCTION	11
1.1 Scope of the Report	11
1.2 Structure of the Report	11
2. PROJECT BACKGROUND.....	12
2.1 Background	12
2.2 Scope of the Project and Site Description	12
2.3 Division of the Project Responsibility	13
2.4 Project Organization and Contact Personnel.....	15
2.5 Principal Work and Activities.....	16
3. MONITORING REQUIREMENTS	19
3.1. Noise Monitoring.....	19
3.2. Air Monitoring	21
3.3 Water Quality Monitoring	23
4. MONITORING RESULTS.....	29
4.1. Noise Monitoring Results.....	29
4.2. Real Time Noise Monitoring Results.....	31
4.3. Air Monitoring Results	32
4.4 Water Monitoring Results	34
4.5 Waste Monitoring Results.....	40
5. COMPLIANCE AUDIT	45
5.1. Noise Monitoring.....	45
5.2. Real-time Noise Monitoring.....	45
5.3. Air Monitoring	45
5.4. Water Quality Monitoring	45
5.5. Site Audit	47
5.6. Review of the Reasons for and the Implications of Non-compliance	47
5.7. Summary of action taken in the event of and follow-up on non-compliance	47
6. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION.....	49
7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS...	50
8. CONCLUSION	51

LIST OF TABLES

Table I	<i>Principal Work Activities for Contract no. HK/2009/01</i>
Table II	<i>Principal Work Activities for Contract no. HK/2009/02</i>
Table III	<i>Principal Work Activities for Contract no. HY/2009/15</i>
Table IV	<i>Principal Work Activities for Contract no. HY/2009/19</i>
Table V	<i>Principal Work Activities for Contract no. HK/2012/08</i>
Table VI	<i>Principal Work Activities for Contract no. HY/2010/08</i>
Table 2.1	<i>Schedule 2 Designated Projects under this Project</i>
Table 2.2	<i>Details of Individual Contracts under the Project</i>
Table 2.3	<i>Contact Details of Key Personnel</i>
Table 2.4	<i>Principal Work Activities for Contract no. HK/2009/01</i>
Table 2.5	<i>Principal Work Activities for Contract no. HK/2009/02</i>
Table 2.6	<i>Principal Work Activities for Contract no. HY/2009/15</i>
Table 2.7	<i>Principal Work Activities for Contract no. HY/2009/19</i>
Table 2.8	<i>Principal Work Activities for Contract no. HK/2012/08</i>
Table 2.9	<i>Principal Work Activities for Contract no. HY/2010/08</i>
Table 3.1	<i>Noise Monitoring Stations</i>
Table 3.2	<i>Real Time Noise Monitoring Station</i>
Table 3.3	<i>Air Monitoring Stations</i>
Table 3.4	<i>Marine Water Quality Stations for Water Quality Monitoring</i>
Table 3.5	<i>Marine Water Quality Monitoring Frequency and Parameters</i>
Table 3.6	<i>Marine Water Quality Stations for Enhanced Water Quality Monitoring</i>
Table 4.1	<i>Noise Monitoring Station for Contract nos. HK/2009/01 and HK/2009/02</i>
Table 4.2	<i>Noise Monitoring Station for Contract nos. HY/2009/15</i>
Table 4.3	<i>Noise Monitoring Stations for Contract no. HY/2009/19</i>
Table 4.4	<i>Noise Monitoring Stations for Contract no. HY/2010/08</i>
Table 4.5	<i>Real Time Noise Monitoring Station for Contract no. HY/2009/19</i>
Table 4.6	<i>Air Monitoring Stations for Contract no. HK/2009/01</i>
Table 4.7	<i>Air Monitoring Station for Contract no. HK/2009/02</i>
Table 4.8	<i>Air Monitoring Station for Contract no. HY/2009/15</i>
Table 4.9	<i>Air Monitoring Stations for Contract no. HY/2009/19</i>
Table 4.10	<i>Water Monitoring Stations for Contract no. HK/2009/01</i>
Table 4.11	<i>Water Monitoring Stations for Contract no. HK/2009/02</i>
Table 4.12	<i>Water Monitoring Stations for Contract no. HK/2012/08</i>
Table 4.13	<i>Water Monitoring Stations for Contract no. HY/2009/15</i>
Table 4.14	<i>Summary of Water Quality Monitoring Exceedances in Reporting period</i>
Table 4.15	<i>Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting period</i>
Table 4.16	<i>Details of Waste Disposal for Contract no. HK/2009/01</i>
Table 4.17	<i>Details of Waste Disposal for Contract no. HK/2009/02</i>
Table 4.18	<i>Details of Waste Disposal for Contract no. HY/2009/15</i>
Table 4.19	<i>Details of Waste Disposal for Contract no. HY/2009/19</i>
Table 4.20	<i>Details of Waste Disposal for Contract no. HK/2012/08</i>
Table 4.21	<i>Details of Waste Disposal for Contract no. HY/2010/08</i>
Table 5.1	<i>Summary of Water Quality Monitoring Exceedances in Reporting period</i>
Table 5.2	<i>Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting period</i>
Table 6.1	<i>Cumulative Statistics on Complaints</i>
Table 6.2	<i>Cumulative Statistics on Successful Prosecutions</i>



LIST OF FIGURES

<u>Figure 2.1</u>	Project Layout
<u>Figure 2.2</u>	Project Organization Chart
<u>Figure 3.1</u>	Locations of Environmental Monitoring Stations

LIST OF APPENDICES

<u>Appendix 2.1</u>	Environmental Mitigation Implementation Schedule
<u>Appendix 3.1</u>	Action and Limit Level
<u>Appendix 4.1</u>	Noise Monitoring Graphical Presentations
<u>Appendix 4.2</u>	Air Quality Monitoring Graphical Presentations
<u>Appendix 4.3</u>	Water Quality Monitoring Graphical Presentations
<u>Appendix 4.4</u>	Real-time Noise Monitoring Results and Graphical Presentations
<u>Appendix 5.1</u>	Event Action Plans
<u>Appendix 6.1</u>	Complaint Log
<u>Appendix 7.1</u>	Construction Programme of Individual Contracts

EXECUTIVE SUMMARY

- i. This is the Quarterly Environmental Monitoring and Audit (EM&A) Report – [March 2015 to May 2015](#) prepared for the Project of Wan Chai Development Phase II and Central-Wanchai Bypass under Environmental Permit no. EP-356/2009 and Further Environmental permit nos. FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009 and FEP-07/356/2009. This report presents the environmental monitoring and audit findings and information during the period from [March 2015 to May 2015](#). The cut-off date of reporting is at 27th of each reporting period.

Construction Activities for the Reported Period

- ii. During this reporting period, the principal work activities for Contract no. HK/2009/01 are summarized as below:

Table I Principal Work Activities for Contract no. HK/2009/01

March 2015	April 2015	May 2015
• Nil	• Nil	• Nil

- iii. During this reporting period, the principal work activities for Contract no. HK/2009/02 are summarized as below:

Table II Principal Work Activities for Contract no. HK/2009/02

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> • Works of covered walkway • ABWF work • Extraction of piles at WCR3 • Air lifting operation at WCR3 	<ul style="list-style-type: none"> • Construction of sewage system • ABWF work • Air lifting operation at WCR3 • Fabrication of slotted panels 	<ul style="list-style-type: none"> • Construction of sewage system • Air lifting operation at WCR3 • Fabrication of slotted panels

- iv. Contract no. HY/2009/15 was commenced on 10 November 2010. During this reporting period, the principal work activities for Contract no. HY/2009/15 are summarized as below:

Table III Principal Work Activities for Contract no. HY/2009/15

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> • Reinstatement of vertical seawall at TS4 • Reinstatement of existing seawall at TPCWAE 	<ul style="list-style-type: none"> • Reinstatement of vertical seawall at TPCWAE 	<ul style="list-style-type: none"> • Reinstatement of vertical seawall at TPCWAE • Dredging work near Noon Day Gun

- v. Contract no. HY/2009/19 was commenced on 24 March 2011. During this reporting period, the principal work activities for Contract no. HY/2009/19 are summarized as below:

Table IV Principal Work Activities for Contract no. HY/2009/19

March 2015	April 2015	May 2015
• Nil	• Nil	• Nil

- vi. Contract no. HK/2012/08 was commenced on 5 March 2013. During this reporting period, the principal work activities for Contract no. HK/2012/08 are summarized as below:

Table V Principal Work Activities for Contract no. HK/2012/08

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> Placing of levelling stones Dry dock construction Pre-bored H-pile construction on temporary piling platform Removal of rock armour 	<ul style="list-style-type: none"> Placing of armour and bermstone Dry dock construction Pre-bored H-pile construction on temporary piling platform 	<ul style="list-style-type: none"> Placing of armour and bermstone Dry dock construction Installation of pipe pile wall

- vii. Contract no. HY/2010/08 was commenced on 21 March 2013. During this reporting period, the principal work activities for Contract no. HY/2010/08 are summarized as below:

Table VI Principal Work Activities for Contract no. HY/2010/08

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> Rock filling works Seawall blocks installation works Pre-treatment works Bar fixing works Diaphragm Wall, Barrette and King Post construction works Fill Disposal works 	<ul style="list-style-type: none"> Rock filling works Seawall blocks installation works Pre-treatment works Bar fixing works Diaphragm Wall, Barrette and King Post construction works Fill Disposal works 	<ul style="list-style-type: none"> Rock filling works Pre-treatment works Bar fixing works ELS works Diaphragm Wall, Barrette construction and King Post installation works Slurry and fill disposal works

Noise Monitoring

- viii. Noise monitoring during day time and evening time were conducted at the M1a, M2b, M3a, M4b, M5b and M6 on a weekly basis in the reporting period. The Action and Limit level exceedances recorded in the reporting period are listed below. Investigation found that exceedances were not related to the Project. Investigation found that exceedances were not related to the Project.
- ix. No action and limit level exceedance was recorded in March reporting month.
- x. One limit level exceedances at M6 – HK Baptist Church Henrietta Secondary School was recorded 21 April 2015 in April reporting month. The exceedance was concluded as non-project related.

- xi. Two limit level exceedances at M6 – HK Baptist Church Henrietta Secondary School were recorded on 5 and 27 May 2015 in May reporting month. The exceedance were concluded as related to Project works.

Real-time Noise Monitoring

- xii. As the land-based piling and filling works- DP3 at Tin Hau had been completed on 3 September 2012 and confirmed by RSS, the real-time noise monitoring results at FEHD Hong Kong Transport Section Whitfield Depot was excluded under EP-356/2009 since 28 November 2012.
- xiii. Real-time noise monitoring at FEHD Hong Kong Transport Section Whitefield Depot and Oil Street Community Centre have been commenced on 5 October 2010 for the filling works of Contract no. HY/2009/11.
- xiv. Real-time noise monitoring at FEHD Hong Kong Transport Section Whitefield Depot commenced external wall renovation since 1 June 2012
- xv. Oil Street Community Liaison Centre was confirmed to be demolished in mid-October by CWB RSS. This presented a need for relocation of RTN2 – Oil Street Community Liaison Centre. After liaison with Hong Kong Electric, permission was granted on 21 Sep 2012 for real time noise monitoring set up at City Garden Electric Centre (RTN2a – Electric Centre), which is a representative of the noise sensitive receiver City Garden. The real-time noise monitoring at RTN2-Oil Street Community Liaison Centre has been relocated to City Garden Electric Centre (RTN2a- Electric Centre) on 5 Oct 2012. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted in Electric Centre from 4 December 2009 to 17 December 2009.
- xvi. No project related exceedance was recorded in March, April and May reporting months at RTN2a-Hong Kong Electric Centre during this reporting quarter.

Air Quality Monitoring

- xvii. Due to electricity interruption, the following 24hr and 1hr TSP monitoring events were rescheduled in this reporting quarter,
24hr TSP monitoring at CMA1b was rescheduled from 23 March 2015 to 24 March 2015 respectively.
24hr TSP monitoring at CMA3a was rescheduled from 23 March 2015 to 25 March 2015.
24hr TSP monitoring at CMA4a was rescheduled from 12 and 23 March 2015 to 13 and 24 March 2015 respectively.
24hr TSP monitoring at CMA5b was rescheduled from 6, 18 and 23 March 2015 to 7, 20 and 24 March 2015 respectively.
24hr TSP monitoring at CMA1b was rescheduled from 22 May 2015 to 23 May 2015 respectively.
1hr TSP monitoring at CMA5b was rescheduled from 19 March 2015 to 19 and 20 March 2015
- xviii. There were no action level and limit level exceedance of air quality monitoring recorded in this reporting quarter.
- xix. The location ID of air monitoring station CMA1b was updated as Oil Street Site Office in April 2013.

- xx. With respect to the area handover, the air quality monitoring station CMA5a at Children Playgrounds opposite to the Pedestrian Plaza was relocated to the Pedestrian Plaza on 3 December 2014. The station reference and location ID of the air quality monitoring station CMA5a was updated as CMA5b and Pedestrian Plaza respectively.
- xxi. 1hr and 24hr TSP monitoring were conducted at CMA1b, CMA2a, CMA3a, CMA4a, CMA5b and CMA6a in the reporting period.

Water Quality Monitoring

- xxii. Due to the hosting of amber rainstorm warning signal, the water quality monitoring event on 11 May 2015 during ebb tide and 20 May 2015 during flood tide were cancelled.
- xxiii. Due to the detachment of steel mesh hindering the water sampling works within the silt screen, the water quality monitoring at the WQM station P1 on 30 April 2015 during flood tide was cancelled.
- xxiv. With respect to the construction works undertaken at Ex-PCWAW and the forthcoming wet season DO concern, the suspended Enhance DO monitoring within Ex-PCWAW area at the Enhance DO monitoring station Ex-PCWA-SW was resumed on 30 March 2015 at the finely adjusted monitoring location.
- xxv. Action and Limit level of water quality monitoring was transited from dry season to wet season from 1 April 2015.
- xxvi. With respect to the commencement of seawall modification works at Ex-PCWAE and the location of the Enhance DO monitoring stations would form an active construction area, the Enhance DO monitoring at monitoring station EX-PCWA SW and SE were temporarily suspended from 2 March 2015 ebb tide and the monitoring at the location is tentatively to be resumed by early April 2015 to cater for the potential DO concern during Wet Season.
- xxvii. Due to material obstruction at monitoring location and safety consideration on nearby barge lifting operation, the Enhance DO monitoring at monitoring station Ex-PCWA SE on 2 March 2015 during flood tide was cancelled.
- xxviii. As informed by CWB RSS, the operation of the diverted Windsor House cooling intake was commenced on 20 Dec 2014 and the water quality monitoring at monitoring station C7 for Windsor House Cooling water intake was resumed on 22 Dec 2014.
- xxix. Water quality monitoring was conducted at 8 monitoring stations namely WSD19, C1, C7, P1, P3, P4, P5 and RW21-P789 during the reporting period.
- xxx. There were 4 action level and 4 limit level exceedance of turbidity recorded in March reporting month. Investigation found that the exceedances were not related to Project works.
- xxxi. There was no action level and limit level exceedance recorded in April reporting month.
- xxxii. There were no action and 1 limit level of turbidity exceedance recorded, and 1 action and no limit level of suspended solid exceedance recorded in May reporting month. Investigation found that the exceedances were not related to Project works.
- xxxiii. Enhanced DO monitoring at 4 monitoring stations in Causeway Bay Typhoon Shelter and Ex-Public Cargo Works Area was conducted three days per week during the reporting period.
- xxxiv. There were no action level and limit level exceedance of enhanced dissolved oxygen recorded in March reporting month.
- xxxv. There were no action level and 1 limit level exceedance of enhanced dissolved oxygen recorded in April reporting month. Investigation found that the exceedance was not related to Project works.

- xxxvi. There were no action level and 2 limit level exceedance of enhanced dissolved oxygen recorded in May reporting month. Investigation found that the exceedance was not related to the Project works.
- xxxvii. With respect to the commencement of temporary reclamation works and seawall construction at Ex-PCWAW zone and diverted culvert extension, the location of the Enhance DO monitoring stations (Ex-PCWASW and Ex-PCWA SE) were finely adjusted to the PCWAE since 7 November 2014.
- xxxviii. With respect to the commencement of marine dredging works at WCR3 under contract HK/2009/02. The respective water quality monitoring station C1 were associated with HK/2009/01 and HK/2009/02.
- xxxix. As confirmed by CWB RSS, the operation of the pump station for Windsor House Cooling Water was suspended from 22 Oct 2014 for the Windsor House intake cooling intake scheme and temporary supply of freshwater from WSD water mains was provided to cooling water intake. The water quality monitoring for the respective cooling water intake at WQM station C7 was temporarily suspended from 22 Oct 2014.
- xl. With respect to the commencement of filling works at TS3 and the formation of TZ3 reclamation zone, the enhance DO monitoring at Enhance monitoring station C7 was temporarily suspended from 22 Oct 2014.
- xli. As confirmed by WDII RSS and IEC, the cross harbor dredging works have completed since 16 March 2012 while the dredging works for submarine outfall pipeline has completed since 29 November 2011, considering current construction stage and dredging Scenario, the water quality monitoring at stations WSD9 and WSD17 was temporarily suspended since 8 September 2014 flood tide.
- xl.ii. As advised by WDII RSS, the water quality monitoring for WSD21 pump station with respect to HK/2009/02 was switched over to the relocated location since 12 March 2014. According to the EM&A Manual, the water quality monitoring station WSD21 was relocated to station RW21-P789 and the water quality monitoring at station WSD21 was temporarily suspended since 12 March 2014.
- xl.iii. With respect to the switching over of cooling water intake location, the water quality monitoring at the relocated intake station RW21-P789 under HK/2009/02 was commenced since 29 July 2013 and monitoring station C5e and C5w were temporarily suspended and switched over to monitoring station RW21-P789 on 29 July 2013 due to suspension of pump house operation.
- xl.iv. With respect to the commencement of dredging works under HK/2012/08 and the installation of MTR precast protection unit, the enhanced water quality monitoring for Culvert L was temporarily suspended since 24 July 2013.
- xl.v. With respect to the commencement of marine dredging works under contract HY/2010/08. The respective water quality monitoring station C7 were associated with HY/2009/15 and HY/2010/08.
- xl.vi. With respect to the commencement of marine dredging works under contract HK/2012/08/ The respective water quality monitoring station WSD19, P1, P3, P4, and P5 were associated with Contract HK/2012/08 Since September 2013.
- xl.vii. WQM events on 22 April 2013 at monitoring stations C2, C3, C4e and C4w were temporarily suspended. Upon confirmation with WDII RSS and the IEC, water quality monitoring at

- relocated intakes monitoring location P1, P3, P4 and P5 were commenced since 24 April 2013.
- xlvi. Due to the marine piling under Contract no. HY/2009/19 was completed on 4 March 2013, the temporary suspension of impact water quality monitoring at C8 and C9 from 4 March 2013 have been monitored for 4-week period after the completion of marine works to confirm no water deterioration.
- xlv. As confirmed by CWB RSS, the marine piling works under contract HY/2009/19 was confirmed completed by 4 March 2013. The water quality monitoring at the respective monitoring stations C8 and C9 were temporarily suspended since 30 March 2013.
- i. RSS confirmed that all Type III Dredging works under HK/2009/01 have been completed since Oct 2012.
 - ii. Due to the presence of obstacle within the inner silt curtain frame at sampling point, water quality point at C7 was finely adjusted to the outside of the inner silt curtain frame since 29 Dec 2012.
 - iii. With respect to the trial dredging at WCR2 was scheduled on 20, 22, 24, 25 March and 1, 3, 11, 13, 15, 17, 19, 20 Apr and 3 May 2012, on-going water quality monitoring results at WSD21 during this period was checked and indicated that there was no contribution due to the trial dredging operation. Enhanced review of water quality around WCR2 was also implemented and no deterioration in the water quality was observed.
 - iiii. Due to the access of water monitoring station at WSD19 was blocked by LCSD construction works from 3 April 2012 to 2 May 2012 and lead to the inaccessibility of sampling either land and marine, there is a fine adjustment of the sampling point of WSD 19 since 5 April 2012 to the closest accessible point prior to the completion of the construction activities.
 - lv. WDII/RSS advised that the dredging works for submarine pipeline at Victoria Harbour had been completed in January 2012. Therefore, the concurrent dredging activities at Sewage Pipeline Zone and reclamation shoreline zone TCBR under the EP-356/2009 scenario 2B no longer exist. As such, with reference to Table 5.39 of the EIA Report for Wan Chai Development Phase II and Central-Wan Chai Bypass, the application of silt screen for cooling water intakes for Queensway Government Offices was suspended and the others remain unchanged.
 - lv. Due to the dredging works for Cross Harbour Water Mains from Wan Chai to Tsim Sha Tsui-DP6 was completed on 26 March 2012, the temporary suspension of impact water quality monitoring at WSD7 and WSD20 after 27 April 2012 for the water quality monitoring at WSD7 and WSD20 have been monitored for 4-week period after the completion of DP6 to confirm no water deterioration. Water quality monitoring at WSD10 and WSD15 was temporary suspended while water quality monitoring at WSD9 and WSD17 was implemented with respect to HK/2009/02 from 8 Feb 12 onwards;
 - lvi. Based on the joint inspection on 4 Jan 2012 for the NPR area, the 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8, C9 to confirm no water deterioration with respect to NPR was commenced since 7 Jan 2012 and it was completed on 6 February 2012.
 - lvii. Based on the safety concern when external façade refurbishment was conducted by contractor employed by Provident Centre (C9) between 9 January 2012 to 30 July 2012 which caused to the inaccessibility of sampling either land and marine since 3 Feb 2012, there is a fine adjustment of the sampling location of water quality monitoring at C9 since 10 March

- 2012 to the closest accessible point prior to the completion of the external façade refurbishment work.
- lviii. Water quality monitoring at C8 and C9 have been implemented with respect to HY/2009/19 since the marine bore piling work started on 28 Jan 12.
- lix. In response to the Condition 2.18 of the Environmental Permit no. EP-356/2009 requiring that a silt curtain / impermeable barrier system be installed to channel water discharge flow from Culvert L to locations outside the embayment area, a proposed replacement of the requirement with additional dissolved oxygen monitoring has been conducted at three monitoring stations, namely A, B and C between the eastern seawall of Central Reclamation Phase III and the HKCEC Extension since November 2011 under EP-356/2009 so that DO level between the eastern seawall of Central Reclamation Phase II and the HKCEC extension could be continuously monitored.

Complaints, Notifications of Summons and Successful Prosecutions

- ix. No environmental complaint received in March, April and May reporting months.

1. INTRODUCTION

1.1 Scope of the Report

1.1.1. Lam Geotechnics Limited (LGL) has been appointed to work as the Environmental Team (ET) under Environmental Permit no. EP-356/2009 and Further Environmental permit nos. FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009 and FEP-07/356/2009 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) and in the EM&A Manual of the approved EIA Report for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001).

1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 10.4 of EM&A Manual and “*Environmental Monitoring and Audit Requirements*” under Particular Specification Section 27.

1.1.3. This report documents the finding of EM&A works during the period from [March 2015 to May 2015](#).

1.2 Structure of the Report

Section 1 ***Introduction*** – details the scope and structure of the report.

Section 2 ***Project Background*** – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.

Section 3 ***Monitoring Requirements*** – summarizes all monitoring parameters, monitoring locations, monitoring frequency, duration and action plan.

Section 4 ***Monitoring Results*** – summarizes the monitoring results obtained in the reporting period.

Section 5 ***Compliance Audit*** – summarizes the auditing of monitoring results, all exceedances environmental parameters.

Section 6 ***Complaints, Notification of summons and Prosecution*** – summarizes the cumulative statistics on complaints, notification of summons and prosecution

Section 7 ***Cumulative Construction Impact due to the Concurrent Projects*** – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.

Section 8 ***Conclusion***

2. PROJECT BACKGROUND

2.1 Background

- 2.1.1. “Wan Chai Development phase II and Central-Wan Chai Bypass” and “Central-Wan Chai Bypass and Island Eastern Corridor Link” (hereafter called “the Project”) are Designed Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001) and Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) have been approved on 31 August 2001 and 11 December 2008 respectively.
- 2.1.2. The key purpose of Wan Chai Development Phase II (WDII) is to provide land at Wan Chai North and North Point for construction of the Central-Wan Chai Bypass and Island Eastern Corridor Link (CWB). Land formed under the project will be developed as a world-class waterfront promenade joining that at the new Central waterfront for public enjoyment.
- 2.1.3. There is a compelling and present need for the CWB to provide relief to the very congested east-west Connaught Road Central/Harcourt Road / Gloucester Road Corridor (the Corridor) which is currently operating beyond its capacity. The CWB will provide relief to the existing congestion along the Corridor and cater for the anticipated growth of traffic on Hong Kong Island. Without the CWB and its access roads, there will not be sufficient capacity to serve the heavy traffic demands at both strategic and local levels.

2.2 Scope of the Project and Site Description

- 2.2.1. The Project is located mainly in Wan Chai North, Causeway Bay and North Point, and is demarcated by Gloucester Road and Victoria Park Road to the south, Fenwick Pier Street to the west and Tong Shui Road Interchange to the east, as shown in **Figure 2.1**.
- 2.2.2. The study area encompasses existing developments along the Wan Chai, Causeway Bay and North Point shorelines. Major land uses include the Hong Kong Convention & Exhibition Centre (HKCEC) Extension, the Wan Chai Ferry Pier, the ex-Wan Chai Public Cargo Working Area (ex-PCWA), the Royal Hong Kong Yacht Club (RHKYC), the Police Officers' Club, the Causeway Bay Typhoon Shelter (CBTS) and commercial and residential developments.
- 2.2.3. The scope of the Project comprises:
- Land formation for key transport infrastructure and facilities, including the Trunk Road (i.e. CWB) and the associated slip roads for connection to the Trunk Road and for through traffic from Central to Wan Chai and Causeway Bay. The land formed for the above transport infrastructure will provide opportunities for the development of an attractive waterfront promenade for the enjoyment of the public
 - Reprovisioning / protection of the existing facilities and structures affected by the land formation works mentioned above

- Extension, modification, reprovisioning or protection of existing storm water drainage outfalls, sewerage outfalls and watermains affected by the revised land use and land formation works mentioned above
- Upgrading of hinterland storm water drainage system and sewerage system, which would be rendered insufficient by the land formation works mentioned above
- Provision of the ground level roads, flyovers, footbridges, necessary transport facilities and the associated utility services
- Construction of the new waterfront promenade, landscape works and the associated utility services
- The Trunk Road (i.e. CWB) within the study area and the associated slip roads for connection to the Trunk Road.

2.2.4. The project also contains various Schedule 2 DPs that, under the EIAO, require Environmental Permits (EPs) to be granted by the DEP before they may be either constructed or operated. **Table 2.1** summarises the five individual DPs under this Project. **Figure 2.1** shows the locations of these Schedule 2 DPs.

Table 2.1 Schedule 2 Designated Projects under this Project

Item	Designated Project	EIAO Reference	Reason for inclusion
DP1	Central-Wanchai Bypass (CWB) including its road tunnel and slip roads	Schedule 2, Part I, A.1 and A.7	Trunk road and road tunnel more than 800 m in length
DP2	Road P2 and other roads which are classified as primary/district distributor roads	Schedule 2, Part I, A.1	Primary / district distributor roads
DP3	Reclamation works including associated dredging works	Schedule 2, Part I, C.1 and C.12	Reclamation more than 5 ha in size and a dredging operation less than 100 m from a seawater intake point
DP5	Wan Chai East Sewage Outfall	Schedule 2, Part I, F.5 and F.6	Submarine sewage pipelines with a total diameter more than 1,200 mm and include a submarine sewage outfall
DP6	Dredging for the Cross-harbour Water Mains from Wan Chai to Tsim Sha Tsui	Schedule 2, Part I, C.12	A dredging operation less than 100 m from a seawater intake point

2.3 Division of the Project Responsibility

2.3.1 Due to the multi-contract nature of the Project, the status of permits and/or licences under the individual contract(s) are presented as below:

Contract no. HK/2010/06 – Wan Chai Development Phase II – Central – Wan Chai Bypass over MTR Tsuen Wan Line under FEP-05/356/2009

2.3.2 The construction works were completed and the FEP-05/356/2009 was surrendered by the Contractor on 3 October 2014.

Contract no. HY/2009/11 – Wan Chai Development Phase II – Central – Wan Chai Bypass - North Point Reclamation

- 2.3.3 The construction works were completed and the FEP-01/356/2009 was surrendered by the Contractor on 22 October 2012.
- 2.3.4 Due to the multi-contract nature of the Project, there are a number of contracts sub-dividing the whole works area into different work areas to be commenced. Contractors of individual contracts will be required by the EP holder to apply Further Environmental Permits (FEP) such that the impact monitoring stations are sub-divided accordingly to facilitate the implementation of EM&A programme and to streamline the EM&A reporting for individual FEP holders correspondingly.
- 2.3.5 The details of individual contracts are summarized in **Table 2.2**.

Table 2.2 Details of Individual Contracts under the Project

Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
HK/2009/01	Wan Chai Development Phase II – Central – Wanchai Bypass at Hong Kong Convention and Exhibition Centre	DP3, DP6	23 July 2010
		DP1, DP2	25 August 2011
HK/2009/02	Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East	DP3, DP5	5 July 2010
		DP1	26 April 2011
HY/2009/11	Wan Chai Development Phase II and Central – Wan Chai Bypass – North Point Reclamation	DP3	17 March 2010 (Completed)
HY/2009/15	Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)	DP3	10 November 2010
		DP1	13 July 2011
HK/2010/06	Wan Chai Development Phase II- Central-Wan Chai Bypass over MTR Tsuen Wan Line	DP3	22 March 2011 (Completed)
04/HY/2006	Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street	DP1	September 2010 (Completed)
HY/2009/17	Central - Wan Chai Bypass (CWB) at FEHD Whitfield Depot - Advanced piling works.	DP1	5 October 2010 (Completed)
HY/2009/18	Central - Wan Chai Bypass (CWB) – Central Interchange	DP1	10 March 2014
HY/2009/19	Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link	DP1	24 March 2011
HK/2012/08	Wan Chai Development Phase II Central- Wan Chai Bypass at Wan Chai West	DP1, DP2, DP3	5 March 2013
HY/2011/08	Central-Wan Chai Bypass (CWB) – Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning	DP1	8 October 2014

2.4 Project Organization and Contact Personnel

2.4.1. Civil Engineering and Development Department and Highways Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.

2.4.2. The proposed project organization and lines of communication with respect to environmental protection works are shown in **Figure 2.2**. Key personnel and contact particulars are summarized in **Table 2.3**:

Table 2.3 Contact Details of Key Personnel

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3912 3388	3912 3010
Chun Wo – Leader Joint Venture	Contractor under Contract no. HK/2009/01	Project Manager	Mr. Simon Liu	9304 8355	2587 1878
		Site Agent	Mr. Andy Yu	9648 4896	
		Engineer Manager	Mr. Terry Wong	9757 9846	
		Construction Manager	Mr. Wyman Wong	9627 2467	
		Construction Manager	Mr. Kenneth Chan	9160 3850	
		Environmental Officer	Ms. Wendy Ng	9803 0057	
		Assistant Environmental Engineer	Miss. Connie Chan	6157 7057	
Chun Wo – CRGL Joint Venture	Contractor under Contract no. HK/2009/02	Project Manager	Mr. Alfred Leung	3658-3022	2827 9996
		Quality & Environmental Manager	Mr. C.P. Ho	9191 8856	
China State Construction Engineering (HK) Ltd.	Contractor under Contract no. HY/2009/15	Project Director	Chris Leung	3557 6393	2566 2192
		Site Manager	Y Huo	3557 6368	
		Contractor's Representative	Andrew Wong	3557 6358	
		Contractor's Representative	Gene Cheung	3557 6395	
		Environmental Officer	Andy Mak	3557 6347	

Party	Role	Post	Name	Contact No.	Contact Fax
Chun Wo - CRGL - MBEC Joint Venture	Contractor under Contract no. HY/2009/19	Project Manager	David Lau	3758 8879	2570 8013
		Site Agent	Paul Yu	9456 9819	
		Environmental Manager / Environmental Officer	Eric Fong	6191 9337	
		Construction Manager (Marine)	M.H. Isa	9884 0810	
		Construction Manager (Land)	Andy Chan	9879 4325	
		Construction Manager (Land)	Bear Ding	6483 6198	
		Operation Manager (Land)	Yung Kwok Wah	9834 1010	
China State-Leader JV	Contractor under Contract no. HK/2012/08	Project Director	C. N. Lai	9106 5806	2877 1522
		Project Manager	Eddie Chung	9189 8118	
		Site Agent	Keith Tse	9037 1839	
		Environmental Officer	James Ma	9130 9549	
		Environmental Supervisor	Y. L. Ho	9856 5669	
China State	Contractor under Contract no. HY/2010/08	Project Director	Chris Leung	3467 4299	2566 8061
		Project Manager	Chan Ying Lun	3418 3001	
		Site Agent	Dave Chan	3467 4277	
		Environmental Officer	C.M. Wong	3557 6464	
		Environmental Supervisor	Desmond Ho Tsz Ho	3557 6466	
ENVIRON Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	34652888	34652899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331

2.5 Principal Work and Activities

2.5.1. During this reporting period, the principal work activities for Contract no. HK/2009/01 are summarized in **Table 2.4**.

Table 2.4 Principal Work Activities for Contract no. HK/2009/01

March 2015	April 2015	May 2015
• Nil	• Nil	• Nil

2.5.2. During this reporting period, the principal work activities for Contract no. HK/2009/02 are summarized in **Table 2.5**.

Table 2.5 Principal Work Activities for Contract no. HK/2009/02

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> • Works of covered walkway • ABWF work • Extraction of piles at WCR3 • Air lifting operation at WCR3 	<ul style="list-style-type: none"> • Construction of sewage system • ABWF work • Air lifting operation at WCR3 • Fabrication of slotted panels 	<ul style="list-style-type: none"> • Construction of sewage system • Air lifting operation at WCR3 • Fabrication of slotted panels

2.5.3. Major construction activities for Contract no. HY/2009/15 was commenced on 10 November 2010. During this reporting period, the principal work activities for Contract no. HY/2009/15 are summarized as below:

Table 2.6 Principal Work Activities for Contract no. HY/2009/15

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> • Reinstatement of vertical seawall at TS4 • Reinstatement of existing seawall at TPCWAE 	<ul style="list-style-type: none"> • Reinstatement of vertical seawall at TPCWAE 	<ul style="list-style-type: none"> • Reinstatement of vertical seawall at TPCWAE • Dredging work near Noon Day Gun

2.5.4. Contract no. HY/2009/19 was commenced on 24 March 2011. During this reporting period, the principal work activities for Contract no. HY/2009/19 are summarized as below:

Table 2.7 Principal Work Activities for Contract no. HY/2009/19

March 2015	April 2015	May 2015
• Nil	• Nil	• Nil

2.5.5. Contract no. HK/2012/08 was commenced on March 2013. During this reporting period, the principal work activities for Contract no. HK/2012/08 are summarized as below:

Table 2.8 Principal Work Activities for Contract no. HK/2012/08

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> • Placing of levelling stones 	<ul style="list-style-type: none"> • Placing of armour and bermstone 	<ul style="list-style-type: none"> • Placing of armour and bermstone

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> • Dry dock construction • Pre-bored H-pile construction on temporary piling platform • Removal of rock armour 	<ul style="list-style-type: none"> • Dry dock construction • Pre-bored H-pile construction on temporary piling platform 	<ul style="list-style-type: none"> • Dry dock construction • Installation of pipe pile wall

2.5.6. Contract no. HY/2010/08 was commenced on 21 March 2013. During this reporting period, the principal work activities for Contract no. HY/2010/08 are summarized as below:

Table 2.9 Principal Work Activities for Contract no. HY/2010/08

March 2015	April 2015	May 2015
<ul style="list-style-type: none"> • Rock filling works • Seawall blocks installation works • Pre-treatment works • Bar fixing works • Diaphragm Wall, Barrette and King Post construction works • Fill Disposal works 	<ul style="list-style-type: none"> • Rock filling works • Seawall blocks installation works • Pre-treatment works • Bar fixing works • Diaphragm Wall, Barrette and King Post construction works • Fill Disposal works 	<ul style="list-style-type: none"> • Rock filling works • Pre-treatment works • Bar fixing works • ELS works • Diaphragm Wall, Barrette construction and King Post installation works • Slurry and fill disposal works

2.5.7. Implementation status of the recommended mitigation measures during this reporting period is presented in **Appendix 2.1**.

3. MONITORING REQUIREMENTS

3.1. Noise Monitoring

NOISE MONITORING STATIONS

- 3.1.1. The noise monitoring stations for the Project are listed and shown in **Table 3.1** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.1 Noise Monitoring Stations

Station	Description
M1a	Harbour Road Sports Centre
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School

REAL TIME NOISE MONITORING STATIONS

- 3.1.2. The real-noise monitoring stations for the Project are listed and shown in **Table 3.2** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.
- 3.1.3. The real-time noise monitoring at RTN2-Oil Street Community Liaison Centre has been relocated to City Garden Electric Centre (RTN2a- Electric Centre) on 5 Oct 2012, which is a representative of noise sensitive receiver- City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted in Electric Centre from 4 December 2009 to 17 December 2009.
- 3.1.4. As the land-based piling and filling works- DP3 at Tin Hau had been completed on 3 September 2012 and confirmed by RSS, the real-time noise monitoring results at RTN1 - FEHD Hong Kong Transport Section Whitfield Depot was excluded under EP-356/2009 since 28 November 2012.

Table 3.2 Real Time Noise Monitoring Station

District	Station	Description
North Point	RTN2	Oil Street Community Liaison Centre
North Point	RTN2a	Electric Centre

- Real time noise monitoring results and graphical presentation during night time period are for information only.
- RTN2 had been relocated to RTN2a since 5 Oct 2012

NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 3.1.5. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). L_{eq} (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, L_{eq} (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L10 and L90 shall also be obtained for reference.
- 3.1.6. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
- one set of measurements between 0700 and 1900 hours on normal weekdays.
- 3.1.7. If construction works are extended to include works during the hours of 1900 – 0700 as well as public holidays and Sundays, additional weekly impact monitoring shall be carried out during respective restricted hours periods. Applicable permits under NCO shall be obtained by the Contractor.
- 3.1.8. Real time noise shall be carried out at the designated monitoring stations. The following is an initial guide on the regular monitoring frequency for each station on a 24 hours daily basis when noise generating activities are underway:
- One set of measurements between 0700 and 1900 hours on normal weekdays.
 - One set of measurements between 1900 and 2300 hours on normal weekdays and 0700 and 2300 hours on public holidays.
 - One set of measurements between 2300 and 0700 hours on next day on everyday.

MONITORING EQUIPMENT

- 3.1.9. As referred to in the Technical Memorandum TM issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.
- 3.1.10. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

3.2. Air Monitoring

AIR QUALITY MONITORING STATIONS

- 3.2.1. The air monitoring stations for the Project are listed and shown in **Table 3.3** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.3 Air Monitoring Stations

Station ID	Monitoring Location	Description
CMA1b	Oil Street Site Office**	North Point
CMA2a	Causeway Bay Community Centre	Causeway Bay
CMA3a	CWB PRE Site Office *	Causeway Bay
CMA4a	Society for the Prevention of Cruelty to Animals	Wan Chai
CMA5b	Pedestrian Plaza***	Wan Chai
CMA6a	WDII PRE Site Office *	Wan Chai

* Remarks: As per the ENPC meeting in January 2011, the monitoring stations CMA3a - Future CWB site office at Wanchai Waterfront Promenade and CMA6a - Future AECOM site office at Work Area were renamed as remark.

Remarks**: The location ID of monitoring station CMA1b was updated as "Oil Street Site Office" in April 2013.

Remarks***: The station ID and monitoring location was updated in December 2014 with respect to monitoring station relocation.

AIR MONITORING PARAMETERS, FREQUENCY AND DURATION

- 3.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 3.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 3.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 3.2.5 High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:

- 0.6 - 1.7 m³ per minute adjustable flow range;
- equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
- installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
- capable of providing a minimum exposed area of 406 cm²;
- flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
- equipped with a shelter to protect the filter and sampler;
- incorporated with an electronic mass flow rate controller or other equivalent devices;
- equipped with a flow recorder for continuous monitoring;
- provided with a peaked roof inlet;
- incorporated with a manometer;
- able to hold and seal the filter paper to the sampler housing at horizontal position;
- easily changeable filter; and
- capable of operating continuously for a 24-hour period.

3.2.6 Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

LABORATORY MEASUREMENT / ANALYSIS

3.2.7 A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.

3.2.8 An alternative non-HOKLAS accredited laboratory was set-up for carrying out the laboratory analysis, the laboratory equipment was approved by the ER on 8 February 2011 and the measurement procedures were witnessed by the IEC. Any measurement performed by the laboratory was demonstrated to the satisfaction of the ER and IEC. IEC shall regularly audit to the measurement performed by the laboratory to ensure the accuracy of measurement results.

3.2.9 Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.

3.2.10 After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.

3.2.11 All the collected samples shall be kept in a good condition for 6 months before disposal.

IMPACT MONITORING FOR ODOUR PATROL

- 3.2.12 Odour patrols along the shorelines of Causeway Bay Typhoon Shelter and ex-Wan Chai Public Cargo Working Area when there is temporary reclamation in Causeway Bay Typhoon Shelter and/or in the ex-Wan Chai Public Cargo Working Area, or when there is dredging of the odorous sediment and slime at the south-western corner of the Causeway Bay Typhoon Shelter. Odour patrols will be carried out at bi-weekly intervals during July, August and September by a qualified person of the ET who shall:
- be at least 16 years of age;
 - be free from any respiratory illnesses; and
 - not be allowed to smoke, eat, drink (except water) or use chewing gum or sweets 30 min before and during odour patrol
- 3.2.13 Odour patrol shall be conducted by independent trained personnel / competent persons patrolling and sniffing around the shore as shown in **Figure 3.1** to detect any odour at the concerned hours (afternoon is preferred for higher daily temperature).
- 3.2.14 The qualified person will use the nose (olfactory sensor) to sniff odours at different locations. The main odour emission sources and the areas to be affected by the odour nuisance will be identified.
- 3.2.15 The perceived odour intensity is to be divided into 5 levels which are ranked in the descending order as follows:
- 0 - Not detected. No odour perceived or an odour so weak that it cannot be easily characterized or described;
 - 1 - Slight Identifiable odour, and slight chance to have odour nuisance;
 - 2 - Moderate Identifiable odour, and moderate chance to have odour nuisance;
 - 3 - Strong Identifiable, likely to have odour nuisance;
 - 4 - Extreme Severe odour, and unacceptable odour level.
- 3.2.16 The findings including odour intensity, odour nature and possible odour sources, and also the local wind speed and direction at each location will be recorded. In addition, some relevant meteorological and tidal data such as daily average temperature, and daily average humidity, on that surveyed day will be obtained from the Hong Kong Observatory Station for reference. The Action and Limit levels for odour patrol are shown in **Appendix 3.1**.

3.3 Water Quality Monitoring

- 3.3.1. The EIA Report has identified that the key water quality impact would be associated with the dredging works during the construction phase. Marine water quality monitoring for dissolved oxygen (DO), suspended solid (SS) and turbidity is therefore recommended to be carried out at selected WSD flushing water intakes. The impact monitoring should be carried out during the proposed dredging works to ensure the compliance with the water quality standards.
- 3.3.2. The updated EM&A Manual for EP-356/2009 (Version in March 2011) is approval by EPD on 29 April 2011. As such, the Action Level and Limit Level for the wet season (April –

September) will be effected and applied to the water quality monitoring data from 30 April 2011.

Water Quality Monitoring Stations

- 3.3.3. It is proposed to monitor the water quality at 2 WSD salt water intakes and 7 cooling water intakes along the seafront of the Victoria Harbour. The proposed water quality monitoring stations of the Project are shown in **Table 3.4** and **Figure 3.1**. **Appendix 3.1** shows the established Action/Limit Levels for the monitoring works.

Table 3.4 Marine Water Quality Stations for Water Quality Monitoring

Station Ref.	Location	Easting	Northing
WSD Salt Water Intake			
WSD19	Sheung Wan	833415.0	816771.0
Cooling Water Intake			
C1	HKCEC Extension	835885.6	816223.0
C7	Windsor House	837193.7	816150.0
P1	HKCEC Phase I	835774.7	816179.4
P3	The Academy of performing Arts	835824.6	816212.0
P4	Shui on Centre	835865.6	816220.0
P5	Government Buildings (Wanchai Tower / Revenue Tower / Immigration Tower)	835895.2	816215.2
Cooling Water Intake / WSD Salt Water Intake			
RW21-P789	Great Eagle Centre/ Sun Hung Kai Centre/ WSD Wanchai salt water intake	836268.0	816020.0

- Remarks: - The cessation of seawater intake operation for C6 was confirmed on 17 May 2011, the water monitoring at C6 was then terminated since 17 May 2011.
- WSD9 and WSD17 were implemented with respect to HK/2009/02 from 8 Feb 2012.
 - 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8, C9 were completed on 6 Feb 2012.
 - C8 and C9 were implemented with respect to HY/2009/19 from 28 Jan 2012.
 - C8 & C9 was temporary suspended on 30 March 2013 due to the marine works for Contract no. HY/2009/19 had been completed on 4 March 2013
 - WSD7 and WSD20 were temporarily suspended from 27 Apr 2012
 - C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since 24 Apr 2013
 - C5e and C5w water quality monitoring station was temporarily suspended since 29 July 2013
 - WSD21 water quality monitoring station was temporarily suspended since 12 March 2014
 - Maintenance responsibility of silt screen C1, WSD19, P3, P4 and P5 are under Contract HK/2009/01.
 - WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 September 2014 flood tide.

WATER QUALITY PARAMETERS AND FREQUENCY

- 3.3.4. Monitoring of dissolved oxygen (DO), turbidity and suspended solids (SS) shall be carried out at WSD flushing water intakes and cooling water intakes. DO and Turbidity are measured in-situ while SS is determined in laboratory.
- 3.3.5. In association with the water quality parameters, other relevant data shall also be measured, such as monitoring location/position, time, sampling depth, water temperature, pH, salinity, dissolved oxygen (DO) saturation, weather conditions, sea conditions, tidal stage, and any special phenomena and work underway at the construction site etc.
- 3.3.6. The interval between two sets of monitoring should not be less than 36 hours except where there are exceedances of Action and/or Limit Levels, in which case the monitoring frequency will be increased. **Table 3.5** shows the proposed monitoring frequency and water quality parameters. Duplicate in-situ measurements and water sampling should be carried out in each sampling event. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.

Table 3.5 Marine Water Quality Monitoring Frequency and Parameters

Activities	Monitoring Frequency ¹	Parameters ²
During the 4-week baseline monitoring period	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
During marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
After completion of marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity

Notes:

- For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.
- Turbidity should be measured in situ whereas SS should be determined by laboratory.

DISSOLVED OXYGEN AND TEMPERATURE MEASURING EQUIPMENT

- 3.3.7. The instrument should be a portable, weatherproof dissolved oxygen measuring instrument complete with cable, sensor, comprehensive operation manuals, and use a DC power source. It should be capable of measuring:
- a dissolved oxygen level in the range of 0-20 mg/l and 0-200% saturation
 - a temperature of 0-45 degree Celsius
- 3.3.8. It should have a membrane electrode with automatic temperature compensation complete with a cable. Sufficient stocks of spare electrodes and cables should be available for replacement where necessary. (e.g. YSI model 59 meter, YSI 5739 probe, YSI 5795A submersible stirrer with reel and cable or an approved similar instrument).

- 3.3.9. Should salinity compensation not be build-in in the DO equipment, in-situ salinity shall be measured to calibrate the DO equipment prior to each DO measurement.

TURBIDITY MEASUREMENT INSTRUMENT

- 3.3.10 The instrument should be a portable, weatherproof turbidity-measuring instrument complete with comprehensive operation manual. The equipment should use a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0-1000 NTU and be complete with a cable (e.g. Hach model 2100P or an approved similar instrument).

SAMPLER

- 3.3.11 Water sampler comprises a transparent PVC cylinder, with a capacity of not less than 2 litres, and can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth (e.g. Kahlsico Water Sampler or an approved similar instrument).

SAMPLE CONTAINER AND STORAGE

- 3.3.12 Water samples for suspended solids measurement should be collected in high-density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to ALS Technichem (HK) Pty Ltd. as soon as possible after collection for analysis.

WATER DEPTH DETECTOR

- 3.3.13 A portable, battery-operated echo sounder shall be used for the determination of water depth at each designated monitoring station. This unit can either be handheld or affixed to the bottom of the workboat, if the same vessel is to be used throughout the monitoring programme.

SALINITY

- 3.3.14 A portable salinometer capable of measuring salinity in the range of 0-40 ppt shall be provided for measuring salinity of the water at each of monitoring location.

MONITORING POSITION EQUIPMENT

- 3.3.15 A hand-held or boat-fixed type digital Global Positioning System (GPS) with waypoint bearing indication or other equivalent instrument of similar accuracy shall be provided and used during monitoring to ensure the monitoring vessel is at the correct location before taking measurements.

CALIBRATION OF IN-SITU INSTRUMENTS

- 3.3.16 All in-situ monitoring instrument shall be checked, calibrated and certified by a laboratory accredited under HOKLAS or equivalent before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the water quality monitoring. Responses of sensors and electrodes should be checked with certified standard solutions before each use. Wet bulb calibration for a DO meter shall be carried out before measurement at each monitoring location.

- 3.3.17 For the on site calibration of field equipment by the ET, the BS 127:1993, "Guide to Field and on-site test methods for the analysis of waters" should be observed.
- 3.3.18 Sufficient stocks of spare parts should be maintained for replacements when necessary. Backup monitoring equipment shall also be made available so that monitoring can proceed uninterrupted even when some equipment is under maintenance, calibration, etc.

LABORATORY MEASUREMENT / ANALYSIS

- 3.3.19 Analysis of suspended solids has been carried out in a HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd. Water samples of about 1L shall be collected at the monitoring stations for carrying out the laboratory SS determination. The SS determination work shall start within 24 hours after collection of the water samples. The SS determination shall follow APHA 19ed or equivalent methods subject to the approval of IEC and EPD.

ENHANCED WATER QUALITY MONITORING IN THE EX-WAN CHAI PUBLIC CARGO WORKING AREA AND THE CAUSEWAY BAY TYPHOON SHELTER

- 3.3.20 The enhanced water quality monitoring and audit programme is to avoid aggravation of odour nuisance from seawater arising from temporary reclamation in the ex-Wan Chai Public Cargo Working Area and the Causeway Bay Typhoon Shelter.
- 3.3.21 Dissolved oxygen monitoring at the intakes C6 and C7 in Causeway Bay Typhoon Shelter when there is temporary reclamation in Causeway Bay Typhoon Shelter and at the south-western and south-eastern corners of the ex-Wan Chai Public Cargo Working Area. The proposed water quality monitoring stations of the Project are shown in **Table 3.6** and **Figure 3.1**.

Table 3.6 Marine Water Quality Stations for Enhanced Water Quality Monitoring

Station	Location
C6	Excelsior Hotel
C7	Windsor House
Ex-WPCWA-SW	South-western of the ex-Wan Chai Public Cargo Working Area
Ex-WPCWA-SE	South-eastern of the ex-Wan Chai Public Cargo Working Area

- 3.3.22 The monitoring of dissolved oxygen are to be carried out 3 days per week, at mid-flood and mid-ebb tides for 3 water depths (1m below water surface, mid-depth and 1m above sea bed, except where the water depth less than 6m, the mid-depth may be omitted. If the water depth be less than 3m, only the mid-depth will be monitored).

DAILY SS MONITORING AND 24 HOURS TURBIDITY MONITORING SYSTEM

- 3.3.23 During dredging of the sediment at the south-western corner of the Causeway Bay Typhoon Shelter, daily monitoring of suspended solids and 24 hour monitoring of turbidity at the cooling water intakes (C6 and C7) shall be conducted.
- 3.3.24 The 24 hours monitoring of turbidity at the cooling water intakes (C6 and C7) shall be established by setting up a continuous water quality monitoring station in front of the intakes during the dredging activities. The monitoring system include the turbidity sensor and data logger which is capable of data capturing at every 5 minutes. The data shall be downloaded daily and compared with the Action and Limit level determined during the baseline water quality monitoring at the cooling water intake locations.

ADDITIONAL DISSOLVED OXYGEN MONITORING FOR CULVERT L WATER DISCHARGE FLOW

- 3.3.25 In response to the Condition 2.18 of the Environmental Permit no. EP-356/2009 requiring that a silt curtain / impermeable barrier system be installed to channel water discharge flow from Culvert L to locations outside the embayment area, a proposed replacement of the requirement with additional dissolved oxygen monitoring has been conducted at three monitoring stations, namely A, B and C between the eastern seawall of Central Reclamation Phase III and the HKCEC Extension since November 2011 under EP-356/2009 so that DO level between the eastern seawall of Central Reclamation Phase II and the HKCEC extension could be continuously monitored.
- 3.3.26 With respect to the commencement of dredging works under HK/2012/08 and the installation of MTR precast protection unit, the enhanced water quality monitoring for Culvert L was temporarily suspended since 24 July 2013
- 3.3.27 The monitoring of dissolved oxygen are to be carried out once per week, at mid-flood and mid-ebb tides for 3 water depths (1m below water surface, mid-depth and 1m above sea bed, except where the water depth less than 6m, the mid-depth may be omitted. If the water depth be equal to or less than 3m, only the mid-depth will be monitored).

4. MONITORING RESULTS

4.0.1. The environmental monitoring will be implemented based on the division of works areas of each designed project managed under different contracts with separate FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in [Figure 2.1](#) and [Figure 3.1](#). The monitoring results are presented in according to the Individual Contract(s).

4.0.2 According to EP-364/2009/A Part B, "Scale and Scope of Designated Project", Remarks (c), "The permanent and temporary reclamation and associated dredging works related to the CWB construction are separately covered by environmental permit No. EP-356/2009 issued to Civil Engineering and Development Department", and marine piling works to be conducted by the Contractor of Contract no. HY/2009/19 from 28 January 2012 was considered to be governed under EP-356/2009. As the construction site area of Contract no. HY/2009/11 had already been handed over to Contract no. HY/2009/19, the designated noise, water and air quality monitoring stations for Contract no. HY/2009/11 would be shared with Contract no. HY/2009/19 from 28 January 2012.

4.1. Noise Monitoring Results

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC and Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

4.1.1. The proposed divisions of noise monitoring stations are summarized in **Table 4.1** below.

Table 4.1 Noise Monitoring Station for Contract nos. HK/2009/01 and HK/2009/02

Station	Description
M1a	Harbour Road Sports Centre

4.1.2. No action or limit level exceedance was recorded in this reporting quarter.

Noise monitoring results measured in this reporting period are reviewed and summarized. Details of graphical presentation can be referred in [Appendix 4.1](#).

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

4.1.3. The noise monitoring for HY/2009/15 was commenced on 10 November 2010. The proposed division of noise monitoring stations are summarized in **Table 4.2** below.

Table 4.2 Noise Monitoring Station for Contract nos. HY/2009/15

Station	Description
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station

4.1.4. No action or limit level exceedance was recorded in this report quarter.

Noise monitoring results measured in this reporting period are reviewed and summarized. Details of graphical presentation can be referred in **Appendix 4.1**.

Contract no. HY/2009/19 – Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 4.1.5. Noise quality monitoring at M4b and M5b have been implemented with respect to HY/2009/19 since the marine bore piling work started on 28 Jan 2012.
- 4.1.6. The proposed division of noise monitoring stations for Contract no. HY/2009/19 are summarized in **Table 4.3** below:

Table 4.3 Noise Monitoring Stations for Contract no. HY/2009/19

Station	Description
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School

- 4.1.7. No action or limit level exceedance was recorded in March reporting month.
- 4.1.8. One limit level exceedance was recorded on 21 April 2015 in April reporting month.
- 4.1.9. Traffic noise was observed during monitoring on 21 April 2015 and it was considered as the major noise contribution. As such, the limit level exceedances were concluded as non-project related.
- 4.1.10. Two limit level exceedance was recorded on 5 and 27 May 2015 in May reporting month.
- 4.1.11. IEC bridge deck saw cutting works under HY/2009/19 was observed during monitoring on 5 May 2015 and no noise mitigation measures was provided for the concerned works. The saw cutting works was considered as the major noise contribution and the limit level exceedance was concluded as Project related. Mitigation measures including the use of movable noise barrier for the saw cutting machine was committed by the Contractor as the CWB RSS confirmed the concerned construction works at the concerned section was temporarily completed on 5 May 2015 and tentatively to be resumed in June 2015. Additional noise monitoring was conducted and no further exceedance was identified.
- 4.1.12. IEC bridge deck saw cutting works under HY/2009/19 was observed during monitoring on 21 May 2015 and single noise barrier was provided to the saw cut machine. The mitigation measures was considered inadequate based on the Contractor submitted rectification proposal and the noise level measured. The saw cutting works was considered as the major noise contribution and the limit level exceedance was concluded as Project related. Mitigation measures including provision of additional movable noise barriers for the saw cutting machine

was implemented by the Contractor and additional noise monitoring was conducted and no further exceedance was identified.

- 4.1.13. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of graphical presentation can be referred in [Appendix 4.1](#).

Contract no. HY/2010/08-Central-Wanchi Bypass Tunnel (Slip Road 8 Section)

- 4.1.14. The proposed division of noise monitoring stations are summarized in **Table 4.4** below.

Table 4.4 Noise Monitoring Station for Contract no. HY/2010/08

Station	Description
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station

- 4.1.15. No action or limit level exceedance was recorded in the reporting quarter.
- 4.1.16. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in [Appendix 4.1](#).

4.2. Real Time Noise Monitoring Results

Contract no. HY/2009/19 – Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 4.2.1 As the land-based piling and filling works- DP3 at Tin Hau had been completed on 3 September 2012 and confirmed by RSS, the real-time noise monitoring results at FEHD Hong Kong Transport Section Whitfield Depot was excluded under EP-356/2009 since 28 November 2012.
- 4.2.2 The real-time noise monitoring at RTN2-Oil Street Community Liaison Centre has been relocated to City Garden Electric Centre (RTN2a- Electric Centre) on 5 Oct 2012, which is a representative of noise sensitive receiver- City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted in Electric Centre from 4 December 2009 to 17 December 2009.
- 4.2.3 The major work activities for Contract no. HY/2009/11 was confirmed substantial complete by RSS on 4 January 2012. The construction site was handed over to contractor HY/2009/19 on 31 December 2011 and the FEP-01/356/2009 was surrendered on 22 Oct 2012.
- 4.2.4 Real-time noise monitoring at FEHD Hong Kong Transport Section Whitfield Depot commenced external wall renovation since 1 June 2012

Table 4.5 Real Time Noise Monitoring Station for Contract no. HY/2009/19

District	Station	Description
North Point	RTN2a	Electric Centre

- Real time noise monitoring results and graphical presentation during night time period are for information only.
- RTN2 had been relocated to RTN2a since 5 Oct 2012
- RTN1 monitoring had been finished on 28 Nov 2012

4.2.5 Limit level exceedances were recorded at RTN2a-Electric Centre during daytime on 28 February 2015 and 3, 4, 5, 6, 7 and 9 March 2015 and 26 March 2015 during day time in the reporting month. After checking with Contractor of HY/2009/19, trench excavation and sheet piling works were undertaken by the Contractor and noise mitigation measures including erection of noise blanket was implemented by the Contractor while breaking works and excavation works was observed across March 2015 at the construction site located next to the concerned monitoring station. In view of the above, the exceedances were considered to be non-Project related and contributed by nearby non-CWB construction site works.

4.2.6 Limit level exceedances were recorded at RTN2a-Electric Centre during daytime on 31 March, 2, 8, 9, 10 and 11 April 2015 during day time in the reporting month. After checking with Contractor of HY/2009/19, sheet-pile driving works were conducted on 31 March 2015 and 2 April 2015 while sheet-pile extraction works were conducted on 8, 9, 10 and 11 April 2015. Noise mitigation measures including erection of noise blanket was implemented by the Contractor while breaking works and excavation works were observed across the concerned period at the construction site located next to the monitoring station. In view of the above, the exceedances were considered to be non-Project related and contributed by nearby non-CWB construction site works.

4.2.7 Limit level exceedances were recorded at RTN2a-Electric Centre during daytime on 19 May 2015 during day time in the reporting month. After checking with Contractor of HY/2009/19, U beam lifting works with trailers and crawler cranes was conducted while breaking works and excavation works was noted on-going at the construction site located next to the monitoring station. In view of the above, the exceedances were considered to be non-Project related and contributed by nearby non-CWB construction site works.

4.3. Air Monitoring Results

4.3.1. 1hr and 24hr TSP monitoring were conducted at CMA1b, CMA2a, CMA3a, CMA4a, CMA5b and CMA6a in the reporting period.

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

4.3.2. Air monitoring was commenced on 1 April 2011 in response to the commencement of the land-filling work for Contract no. HK/2009/01. The proposed division of air monitoring stations are summarized in **Table 4.6** below.

Table 4.6 Air Monitoring Stations for Contract no. HK/2009/01

Station	Description
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office *

- 4.3.3. No action or limit exceedance was recorded in this reporting quarter.

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

- 4.3.4. Air monitoring was commenced in mid-January 2011 for the land-filling work for Contract no. HK/2009/02. The proposed division of air monitoring stations is summarized in **Table 4.7** below.

Table 4.7 Air Monitoring Station for Contract no. HK/2009/02

Station	Description
CMA4a	Society for the Prevention of Cruelty to Animals

- 4.3.5. No action or limit level exceedance was recorded in March, April and May reporting month.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

- 4.3.6. Air monitoring was commenced on 15 March 2011 for the land filling work for Contract no. HY/2009/15. The proposed division of air monitoring stations are summarized in **Table 4.8** below.

Table 4.8 Air Monitoring Station for Contract no. HY/2009/15

Station	Description
CMA3a	CWB PRE Site Office

- 4.3.7. No action or limit exceedance was recorded in this reporting quarter.

Contract no. HY/2009/19 –Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 4.3.8. Air monitoring at CMA1b and CMA2a have been implemented with respect to HY/2009/19 since the marine bore piling works started on 28 Jan 2012. No exceedance was recorded in the reporting period.
- 4.3.9. The proposed division of air monitoring stations is summarized in **Table 4.9** below.

Table 4.9 Air Monitoring Stations for Contract no. HY/2009/19

Station	Description
CMA1b	Oil Street Site Office
CMA2a	Causeway Bay Community Centre

4.3.10. No action or limit exceedance was recorded in this reporting quarter.

4.4 Water Monitoring Results

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

4.4.1. Water quality monitoring for Contract no. HK/2009/01 was commenced on 23 July 2010. The proposed division of water monitoring stations is summarized in **Table 4.10** below.

4.4.2. Water quality monitoring station RW21-P789 has been implemented with respect to HK/2009/02 started on 29 July 2013.

Table 4.10 Water Monitoring Stations for Contract no. HK/2009/01

Station Ref.	Location	Easting	Northing
Cooling Water Intake			
C1	HKCEC Extension	835885.6	816223.0

Remarks:

- The water monitoring stations for the dredging works under Contract No. HK/2009/01 should also include WSD9, WSD17, WSD 21 and C5 if water quality monitoring at these locations have not been carried out by others. Similarly, the water monitoring stations for the dredging works under Contract No. HK/2009/02 should also include WSD7, WSD9, WSD17, WSD 19, C1, C2, C3 and C4 if water quality monitoring at these locations have not been carried out by others.
- WSD7 and WSD20 water quality monitoring were temporarily suspended since 27 Apr 2012.
- C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since 24 Apr 2013

Contract no. HK/2009/02 - Wan Chai Development Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

4.4.3. Water quality monitoring for Contract no. HK/2009/02 was commenced on 8 July 2010. The proposed division of water monitoring stations is summarized in **Table 4.11** below.

Table 4.11 Water Monitoring Stations for Contract no. HK/2009/02

Station Ref.	Location	Easting	Northing
WSD Salt Water Intake			
WSD9	Tai Wan	837921.0	818330.0
WSD17	Quarry Bay	839790.3	817032.2
Cooling Water Intake			
C1	HKCEC Extension	835885.6	816223.0

Station Ref.	Location	Easting	Northing
WSD Salt Water Intake			
WSD9	Tai Wan	837921.0	818330.0
WSD17	Quarry Bay	839790.3	817032.2
Cooling Water Intake			
RW21-P789	Great Eagle Centre/ Sun Hung Kai Centre/CWB	836268.0	816020.0

Remarks:

- The water monitoring stations for the dredging works under Contract No. HK/2009/01 should also include WSD9, WSD17, WSD 21 and C5 if water quality monitoring at these locations have not been carried out by others. Similarly, the water monitoring stations for the dredging works under Contract No. HK/2009/02 should also include WSD7, WSD9, WSD17, WSD 19, C1, C2, C3 and C4 if water quality monitoring at these locations has not been carried out by others.
- Water quality monitoring at WSD9 and WSD 17 was implemented with respect to HK/2009/02 from 8 Feb 2012.
- C5e and C5w water quality monitoring station was temporarily suspended since 29 July 2013
- WSD21 water quality monitoring station was temporarily suspended since 12 March 2014
- WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 September 2014 flood tide.
- The water monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.

Contract no. HK/2012/08 - Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

- 4.4.4. Water monitoring for Contract no. HK/2012/08 was commenced on 5 March 2013. The proposed division of water monitoring stations are summarized in **Table 4.12** below.

Table 4.12 Water Monitoring Stations for Contract no. HK/2012/08

Station Ref.	Location	Easting	Northing
WSD Salt Water Intake			
WSD19	Sheung Wan	833415.0	816771.0
Cooling Water Intake			
P1	HKCEC Phase I	835774.7	816179.4
P3	The Academy of performing Arts	835824.6	816212.0
P4	Shui on Centre	835865.6	816220.0
P5	Government Buildings (Wanchai Tower / Revenue Tower / Immigration Tower)	835895.2	816215.2

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

- 4.4.5. As the removal of reclamation work of TS1 at CBTS has been completed, all procedures have been rectified and complied with the conditions set in EP-356/2009 and FEP-04/356/2009.
- 4.4.6. Due to the presence of obstacle within the inner silt curtain frame at sampling point, water quality point at C7 was finely adjusted to the outside of the inner silt curtain frame since 29 Dec 2012.
- 4.4.7. Due to the commencement of the maintenance dredging on 10 November 2010, water quality monitoring for Contract no. HY/2009/15 was commenced on 9 November 2010. The proposed division of water monitoring stations is summarized in **Table 4.13** below.

Table 4.13 Water Monitoring Stations for Contract no. HY/2009/15

Station Ref.	Location	Easting	Northing
Cooling Water Intake			
C7	Windsor House	837193.7	816150.0

Remarks: - The cessation of seawater intake operation for C6 was confirmed on 17 May 2011, the water monitoring at C6 was then terminated since 17 May 2011.

Contract no. HY/2009/19 – Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 4.4.8. Due to the commencement of the marine bored piling on 28 Jan 2012, water quality monitoring for Contract no. HY/2009/19 was commenced on 28 Jan 2012.
- 4.4.9. Due to the marine piling under Contract no. HY/2009/19 was completed on 4 March 2013, the temporary suspension of impact water quality monitoring at C8 and C9 from 4 March 2013 have been monitored for 4-week period after the completion of marine works to confirm no water deterioration.
- 4.4.10. As confirmed by CWB RSS, the marine piling works under contract HY/2009/19 was confirmed completed by 4 March 2013. The water quality monitoring at the respective monitoring stations C8 and C9 were temporarily suspended since 30 March 2013.
- 4.4.11. Based on the joint inspection on 4 Jan 2012 for the NPR area, the 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8, C9 to confirm no water deterioration with respect to NPR was commenced since 7 Jan 2012 and it was completed on 6 February 2012.
- 4.4.12. Water quality monitoring at WSD10 and WSD15 was temporary suspended while water quality monitoring at WSD9 and WSD17 was implemented with respect to HK/2009/02 from 8 Feb 12 onwards;
- 4.4.13. Water quality monitoring at C8 and C9 have been implemented with respect to HY/2009/19 since the marine bore piling work started on 28 Jan 12.

- 4.4.14. Based on the safety concern when external façade refurbishment was conducted by contractor employed by Provident Center (C9) between 9 January 2012 to 30 July 2012 which caused to the inaccessibility of sampling either land and marine since 3 Feb 2012, there is a fine adjustment of the sampling location of water quality monitoring at C9 since 10 March 2012 to the closest accessible point prior to the completion of the external façade refurbishment work.
- 4.4.15. With respect to the trial dredging at WCR2 was scheduled on 20, 22, 24, 25 March and 1, 3, 11, 13, 15, 17, 19, 20 Apr and 3 May 2012, on-going water quality monitoring results at WSD21 during this period was checked and indicated that there was no contribution due to the trial dredging operation. Enhanced review of water quality around WCR2 was also implemented and no deterioration in the water quality was observed.
- 4.4.16. Due to the access of water monitoring station at WSD19 was blocked by LCSD construction works from 3 April 2012 to 2 May 2012 and lead to the inaccessibility of sampling either land and marine, there is a fine adjustment of the sampling point of WSD 19 since 5 April 2012 to the closest accessible point prior to the completion of the construction activities.
- 4.4.17. Due to the dredging works for Cross Harbour Water Mains from Wan Chai to Tsim Sha Tsui-DP6 was completed on 26 March 2012, the temporary suspension of impact water quality monitoring at WSD7 and WSD20 after 27 April 2012 for the water quality monitoring at WSD7 and WSD20 have been monitored for 4-week period after the completion of DP6 to confirm no water deterioration.
- 4.4.18. As per the meeting with the representative of Excelsior Hotel and World Trade Centre on 17 May 2011, they confirmed that the seawater intake for The Excelsior was no longer in use and replaced by the connected permanent water supply from WSD pipelines since 11 January 2011. Thus, the impact water quality monitoring for the cooling intake - C6 was terminated effective from 26 May 2011.
- 4.4.19. 24 hours monitoring of turbidity at the cooling water intakes at C7 was conducted. With respect to the seawall collapsing at TS4 on 17 November 2011, the 24 hours turbidity monitoring and was kept in November 2011. Since the reinstating the seawall was completed on 13 January 2012 and no any water deterioration was performed, 24 hour turbidity monitoring was then suspended on 27 January 2012.
- 4.4.20. The enhanced water quality monitoring at C6, C7, Ex-WPCWA-SW and Ex-WPCWA-SE was commenced on 13 January 2011.
- 4.4.21. Water monitoring results measured in this reporting period are reviewed and summarized in **Table 4.14**. Details of water quality monitoring results and graphical presentation can be referred in **Appendix 4.3**.

Table 4.14 Summary of Water Quality Monitoring Exceedances in Reporting period

Contract no.	Water Monitoring Station	Mid-flood						Mid-ebb					
		DO		Turbidity		SS		DO		Turbidity		SS	
		AL	LL	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
HK/2009/01 & HK/2009/02	C1	0	0	0	1	0	0	0	0	0	0	0	0
HK/2012/08	WSD19	0	0	0	1	0	0	0	0	2	3	1	0
	P1	0	0	0	0	0	0	0	0	0	0	0	0
	P3	0	0	0	0	0	0	0	0	0	0	0	0
	P4	0	0	0	0	0	0	0	0	0	0	0	0
	P5	0	0	0	0	0	0	0	0	0	0	0	0
HK/2009/02	RW21-P789	0	0	2	0	0	0	0	0	0	0	0	0
HY/2009/15 & HY/2010/08	C7	0	0	0	0	0	0	0	0	0	0	0	0
Total		0	0	2	2	0	0	0	0	2	3	1	0

Remarks:

- The cessation of seawater intake operation for C6 was confirmed on 17 May 2011, the water monitoring at C6 was then terminated since 17 May 2011.
- WSD9 and WSD17 were implemented with respect to HK/2009/02 from 8 Feb 2012.
- 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8 and C9 were completed on 6 Feb 2012.
- C8 and C9 were implemented with respect to HY/2009/19 from 28 Jan 2012.
- C8 & C9 was temporary suspended on 30 March 2013 due to the marine works for Contract no. HY/2009/19 had been completed on 4 March 2013
- WSD7 and WSD20 were temporarily suspended from 27 Apr 2012
- C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since 24 Apr 2013
- C5e and C5w water quality monitoring station was temporarily suspended since 29 July 2013
- WSD21 water quality monitoring station was temporarily suspended since 12 March 2014
- Maintenance responsibility of silt screen C1, WSD19, P3, P4 and P5 are under Contract HK/2009/01.
- WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 September 2014 flood tide.
- Water quality monitoring for Windsor House Cooling (Station Ref: C7) was temporarily suspended since 22 October 2014 with respect to the diversion scheme and was resumed since 22 December 2014.
- The water monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.

4.4.22. There were 4 action level and 4 limit level exceedances of turbidity recorded in March reporting month. Investigation found that the exceedances were not related to Project works.

4.4.23. There were no action level and limit level exceedance recorded in April reporting month.

4.4.24. There was no action and 1 limit level of turbidity exceedance, and 1 action and no limit level of suspended solid exceedance recorded in May reporting month. Investigation found that the exceedances were not related to Project works.

4.4.25. Enhanced DO monitoring at 4 monitoring stations in Causeway Bay Typhoon Shelter and Ex-Public Cargo Works Area was conducted three days per week during the reporting period. The action and limit level exceedances of water quality monitoring are summarized in **Table 4.15**.

Table 4.15 Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting period

Contract no.	Water Monitoring Station	Mid-flood		Mid-ebb	
		DO		DO	
		AL	LL	AL	LL
HY/2009/15	C6	0	0	0	0
	C7	0	0	0	0
	Ex-WPCWA SW	0	0	0	3
	Ex-WPCWA SE	0	0	0	0
Total		0	0	0	3

- 4.4.26. There were no action level and limit level exceedance of enhanced dissolved oxygen recorded in March reporting month.
- 4.4.27. There were no action level and 1 limit level exceedance of enhanced dissolved oxygen recorded in April reporting month. Investigation found that the exceedance was not related to the Project works.
- 4.4.28. There were no action level and 2 limit level exceedances of enhanced dissolved oxygen recorded in May reporting month. Investigation found that the exceedance was not related to the Project works.
- 4.4.29. Investigation found that the exceedances are not related to the Project works. Details of graphical presentation can be referred in **Appendix 4.3.**
- 4.4.30. In response to the Condition 2.18 of the Environmental Permit no. EP-356/2009 requiring that a silt curtain / impermeable barrier system be installed to channel water discharge flow from Culvert L to locations outside the embayment area, a proposed replacement of the requirement with additional dissolved oxygen monitoring has been conducted at three monitoring stations, namely A, B and C between the eastern seawall of Central Reclamation Phase III and the HKCEC Extension since November 2011 under EP-356/2009 so that DO level between the eastern seawall of Central Reclamation Phase II and the HKCEC extension could be continuously monitored.
- 4.4.31. With respect to the commencement of dredging works under HK/2012/08 and the installation of MTR precast protection unit, the enhanced water quality monitoring for Culvert L was temporarily suspended since 24 July 2013
- 4.4.32. With respect to the commencement of temporary reclamation works and seawall construction at Ex-PCWAW zone and diverted culvert extension, the location of the Enhance DO monitoring stations (Ex-PCWASW and Ex-PCWA SE) were finely adjusted to the PCWAE since 7 November 2014.

4.5 Waste Monitoring Results

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

- 4.5.1. No Inert C&D waste and non-inert C&D waste was disposed of for the site works in this reporting period. Details of the waste flow table are summarized in **Table 4.16**.

Table 4.16 Details of Waste Disposal for Contract no. HK/2009/01

Waste Type	Quantity this quarter	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	NIL	62116.405	TKO137, TM38
Inert C&D materials recycled, m ³	NIL	5856.5	N/A
Non-inert C&D materials disposed, m ³	NIL	1673.69	SENT Landfill
Non-inert C&D materials recycled, kg	NIL	203993	N/A
Chemical waste disposed, kg	NIL	10250	N/A
Marine Sediment (Type 1 – Open Sea Disposal) , m ³	NIL (Bulk Volume)	97428.2 (Bulk Volume)	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m ³	NIL (Bulk Volume)	52250 (Bulk Volume)	East of Cha Chau
Dredged Sediment Requiring Type 3 – Special Treatment / Disposal contained in Geosynthetic Containers	NIL (Bulk Volume)	6773 (Bulk Volume)	East of Cha Chau

- 4.5.2. There were no Marine Sediment (Type 1 – Open Sea Disposal) and no Marine Sediment (Type 1- Open Sea Disposal (Dedicate Sites) & Type 2- Confined Marine Disposal) disposed of in this reporting quarter.

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

- 4.5.3. No Inert and non-inert C&D waste were disposed of for the site works in this reporting period. Details of the waste flow table are summarized in **Table 4.17**.

Table 4.17 Details of Waste Disposal for Contract no. HK/2009/02

Waste Type	Quantity this quarter	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	NIL	276075.1	TKO137/ TM 38
Inert C&D materials recycled, m ³	NIL	18161	N/A
Non-inert C&D materials disposed, m ³	NIL	1515.103	SENT Landfill
Non-inert C&D materials recycled, m ³	N/A	N/A	N/A
Chemical waste disposed, kg	NIL	13860	SENT Landfill
Marine Sediment (Type 1 – Open Sea Disposal), m ³ *	1996	243815 (Bulk volume)	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal), m ³ *	0	150873 (Bulk volume)	East of Sha Chau

* Remarks: Contractor clarified the quantity of marine sediment – type 1 open sea disposal for February 2015 reporting month was 3331m³ and the quantity of marine sediment – type 1 open sea disposal (Dedicate Sites) & Type 2- confined marine disposal for February 2015 reporting month was 521m³, hence the cumulative quantity is updated in March reporting month.

- 4.5.4. There were Marine Sediment (Type 1 – Open Sea Disposal) and no Marine Sediment (Type 1- Open Sea Disposal (Dedicate Sites) & Type 2- Confined Marine Disposal) disposed of in this reporting quarter.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

- 4.5.5. No inert and non-inert C&D waste were disposed of for the site works in this reporting period. Details of the waste flow table are summarized in **Table 4.18**.

Table 4.18 Details of Waste Disposal for Contract no. HY/2009/15

Waste Type	Quantity this quarter	Cumulative Quantity-to-Date	Disposal / Dumping Grounds	Remarks
Inert C&D materials disposed, m ³	NIL	141579.2	Tuen Mun Area 38	NIL
	NIL	65216	TKO137 FB	NIL
Inert C&D materials recycled, m ³	NIL	304	Ex-PCWA	NIL
	NIL	111.9	TS4	NIL
Non-inert C&D materials disposed, m ³	NIL	252.2	SENT Landfill	NIL

Waste Type	Quantity this quarter	Cumulative Quantity-to-Date	Disposal / Dumping Grounds	Remarks
Non-inert C&D materials recycled, kg	NIL	299361.5	N/A	NIL
Chemical waste disposed, kg	NIL	8,200	N/A	NIL
Marine Sediment (Type 1 – Open Sea Disposal) , m ³	1090	126298 (Bulk Volume)	South of Cheung Chau	Dredging from TCBR1E / TCBR1W / TCBR2/ TCBR3 / TCBR4 / Maintenance dredging
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m ³	1330	288615 (Bulk Volume)	East of Sha Chau	Dredging from TCBR1E / TCBR1W / TCBR2/ TCBR3 / TCBR4 / Maintenance dredging
Marine Sediment (Type 3 – Special Treatment / Disposal contained in Geosynthetic Containers)	NIL	12640 (Bulk Volume)	East of Sha Chau	Dredging from TCBR1W / Maintenance dredging
Marine Sediment (Type 2 – Confined Marine Disposal), m3	NIL (Bulk Volume)	9350 (Bulk Volume)	East of Sha Chau	Dredging from Eastern Breakwater of CBTS
Marine Sediment (Type 1 – Open Sea Disposal) , m3	NIL (Bulk Volume)	600 (Bulk Volume)	East Sha Chau / South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement
Marine Sediment (Type 2– Confined Marine Disposal) , m3	NIL (Bulk Volume)	14,780 (Bulk Volume)	South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement
Marine Sediment (Type 3 – Special Treatment / Disposal contained in Geosynthetic Containers) , m3	NIL (Bulk Volume)	2,760 (Bulk Volume)	South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement

- 4.5.6. There was Marine Sediment (Type 1 – Open Sea Disposal) and Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) disposed in this reporting quarter.

Contract no. HY/2009/19 – Central- WanChai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 4.5.7. No Inert and non-inert C&D waste were disposed of in this reporting quarter

Table 4.19 Details of Waste Disposal for Contract no. HY/2009/19

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	NIL	355921.04	TM38

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials recycled, m ³	NIL	59367	N/A
Non-inert C&D materials disposed, m ³	NIL	1068.6	N/A
Non-inert C&D materials recycled, kg	NIL	333.14	N/A
Chemical waste disposed, L	NIL	2.12	N/A
Marine Sediment (Type 1 – Open Sea Disposal), m ³	NIL	162	South Cheung Chau
Marine Sediment (Type 2 – Confined Marine Disposal) , m ³	NIL	681	East Sha Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m ³	NIL	4976.00	N/A

- 4.5.8. There were no marine sediments Type1- Open Sea Disposal and there were no Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal in this reporting quarter.

Contract no. HK/2012/08 –Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

- 4.5.9. Inert C&D waste were disposed of in this reporting quarter. Details of the waste flow table are summarized in Table 4.20.

Table 4.20 Details of Waste Disposal for Contract no. HK/2012/08

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	245	4131	TM38
Inert C&D materials recycled, m ³	NIL	NIL	N/A
Non-inert C&D materials disposed, m ³ *	NIL	315	N/A
Non-inert C&D materials recycled, kg	NIL	NIL	N/A
Chemical waste disposed, L	NIL	NIL	N/A
Marine Sediment (Type 1 – Open Sea Disposal), m ³ *	NIL (Bulk volume)	31759 (Bulk volume)	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m ³ *	NIL (Bulk volume)	108485 (Bulk volume)	South of The Brothers (from 27 Aug 2013 onwards)

- 4.5.10. No Marine Sediment (Type 1 – Open Sea Disposal) and no marine sediment Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal generated disposed in this reporting quarter.

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8)

- 4.5.11. No Inert C&D waste and non-inert C&D waste were disposed in this reporting period. Details of the waste flow table are summarized in Table 4.21

Table 4.21 Details of Waste Disposal for Contract no. HY/2010/08

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	1119711.3	119711.3	N/A
Inert C&D materials recycled, m ³	NIL	NIL	N/A
Non-inert C&D materials disposed, m ³	NIL	NIL	N/A
Non-inert C&D materials recycled, kg	NIL	NIL	N/A
Chemical waste disposed, L	NIL	NIL	N/A
Marine Sediment (Type 1 – Open Sea Disposal)	710	55290	South Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine disposal)	NIL	27760	Brothers Island
Marine Sediment (Type 3 – Special Treatment)	NIL	7780	Brothers Island

- 4.5.12. There were Marine Sediment (Type 1 – Open Sea Disposal) disposed in this reporting quarter and no Marine Sediment (Type 3 – Special Treatment) and marine sediment Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal generated disposed in this reporting quarter.

5. COMPLIANCE AUDIT

- 5.0.1. The Event Action Plan for construction noise, air quality and water quality are presented in **Appendix 5.1.**

5.1. Noise Monitoring

- 5.1.1 No action and limit level exceedance was recorded in March reporting period.
- 5.1.2 One limit level exceedance was recorded on 21 April 2015 at M6 – HK Baptist Church Henrietta Secondary School in April reporting month. Investigations found that on 21 April 2015, traffic noise was the major contribution in the noise monitoring and exceedance was not related to the Project.
- 5.1.3 Two limit level exceedances were recorded on 5 and 27 May 2015 at M6 – HK Baptist Church Henrietta Secondary School in May reporting month. Investigations found that on 5 May 2015 and 27 May 2015, IEC bridge deck saw cutting works were the major contribution in the noise monitoring and exceedance were related to the Project works.
- 5.1.4 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of graphical presentation can be referred in **Appendix 4.1.**

5.2. Real-time Noise Monitoring

- 5.2.1 No project related exceedances were recorded in March, April and May reporting month at RTN2a-Hong Kong Electric Centre during this reporting quarter.
- 5.2.2 Details of real time noise monitoring results and graphical presentation can be referred to **Appendix 4.2**

5.3. Air Monitoring

- 5.3.1 No action or limit exceedance was recorded in 1-hr TSP and 24-hrs TSP monitoring in this reporting quarter.

5.4. Water Quality Monitoring

- 5.4.1. The summary of water quality exceedances recorded in reporting period is presented in the **Table 5.1** and **Table 5.2.**

Table 5.1 Summary of Water Quality Monitoring Exceedances in Reporting period

Contract no.	Water Monitoring Station	Mid-flood						Mid-ebb					
		DO		Turbidity		SS		DO		Turbidity		SS	
		AL	LL	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
HK/2009/01 & HK/2009/02	C1	0	0	0	1	0	0	0	0	0	0	0	0
HK/2012/08	WSD19	0	0	0	1	0	0	0	0	2	3	1	0
	P1	0	0	0	0	0	0	0	0	0	0	0	0
	P3	0	0	0	0	0	0	0	0	0	0	0	0
	P4	0	0	0	0	0	0	0	0	0	0	0	0
	P5	0	0	0	0	0	0	0	0	0	0	0	0
HK/2009/02	RW21-P789	0	0	2	0	0	0	0	0	0	0	0	0
HY/2009/15 & HY/2010/08	C7	0	0	0	0	0	0	0	0	0	0	0	0
Total		0	0	2	2	0	0	0	0	2	3	1	0

Remarks:

- The cessation of seawater intake operation for C6 was confirmed on 17 May 2011, the water monitoring at C6 was then terminated since 17 May 2011.
- WSD9 and WSD17 were implemented with respect to HK/2009/02 from 8 Feb 2012.
- 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8 and C9 were completed on 6 Feb 2012.
- C8 and C9 were implemented with respect to HY/2009/19 from 28 Jan 2012.
- C8 & C9 was temporary suspended on 30 March 2013 due to the marine works for Contract no. HY/2009/19 had been completed on 4 March 2013
- WSD7 and WSD20 were temporary suspended since 27 April 2012
- C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since 24 Apr 2013
- C5e and C5w water quality monitoring station was temporarily suspended since 29 July 2013
- WSD21 water quality monitoring station was temporarily suspended since 12 March 2014
- Maintenance responsibility of silt screen C1, WSD19, P3, P4 and P5 are under Contract HK/2009/01.
- WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 September 2014 flood tide.
- Water quality monitoring for Windsor House Cooling (Station Ref: C7) was temporarily suspended since 22 October 2014 with respect to the diversion scheme and was resumed since 22 December 2014
- The water monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.

5.4.2. There were 4 action level and 4 limit level exceedances of turbidity recorded in March reporting month. Investigation found that the exceedances were not related to Project works.

5.4.3. There were no action level and limit level exceedance recorded in April reporting month.

5.4.4. There was no action and 1 limit level of turbidity exceedance, and 1 action and no limit level of suspended solid exceedance recorded in May reporting month. Investigation found that the exceedances were not related to Project works.

Table 5.2 Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting period

Contract no.	Water Monitoring Station	Mid-flood		Mid-ebb	
		DO		DO	
		AL	LL	AL	LL
HY/2009/15	C6	0	0	0	0
	C7	0	0	0	0
	Ex-WPCWA SW	0	0	0	3
	Ex-WPCWA SE	0	0	0	0
Total		0	0	0	3

5.4.5. There were no action level and limit level exceedance of enhanced dissolved oxygen recorded in March reporting month.

5.4.6. There were no action level and 1 limit level exceedance of enhanced dissolved oxygen recorded in April reporting month. Investigation found that the exceedance was not related to the Project works.

5.4.7. There were no action level and 2 limit level exceedances of enhanced dissolved oxygen recorded in May reporting month. Investigation found that the exceedance was not related to the Project works.

5.5. Site Audit

5.5.1. There was no non-compliance from the site audits in the reporting period. During environmental site inspections conducted during the reporting period, minor deficiencies were noted.

5.6. Review of the Reasons for and the Implications of Non-compliance

5.6.1 There was no non-compliance from the site audits in the reporting period.

5.7. Summary of action taken in the event of and follow-up on non-compliance

5.7.1 There was no particular action taken since no project-related non-compliance was recorded from the site audits in March and April reporting months.

5.7.2 One limit level exceedance was recorded on 5 May 2015 at noise monitoring station M6- HK Baptist Church Henrietta Secondary School and was considered in relation to IEC bridge deck saw cutting works under HY/2009/19. Following the Event and Action Plan, additional noise monitoring was conducted and a proposal for remediation measures was submitted by the Contractor. Rectification measures including provision of noise barrier for saw cutting works was committed by the Contractor at the concerned construction works was completed on the same date as confirmed by RSS and no further exceedances was recorded during additional monitoring.

- 5.7.3 One limit level exceedance was recorded on 27 May 2015 at noise monitoring station M6- HK Baptist Church Henrietta Secondary School and was considered in relation to IEC bridge deck saw cutting works under HY/2009/19. Following the Event and Action Plan, additional noise monitoring was conducted and a proposal for remediation measures was submitted by the Contractor. Rectification measures including provision of additional noise barrier for saw cutting works was implemented by the Contractor and no further exceedance was recorded during additional monitoring.

6. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

- 6.0.1. No environmental complaint received in March, April and May reporting months.
- 6.0.2. The details of cumulative complaint log and summary of complaints are presented in **Appendix 6.1**.
- 6.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in **Table 6.1** and **Table 6.2** respectively.

Table 6.1 Cumulative Statistics on Complaints

Reporting Period	No. of Complaints
Commencement works (Mar 2010) to last reporting period	35
March 2015 - May 2015	0
Project-to-Date	35

Table 6.2 Cumulative Statistics on Successful Prosecutions

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this quarter (Offence Date)	Cumulative No. Project-to-Date
Air	-	0	0
Noise	-	0	0
Water	-	0	0
Waste	-	0	0
Total	-	0	0

7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS

- 7.0.1. According to Condition 3.4 of the EP-356/2009, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III, Central-Wanchai Bypass and Island Eastern Corridor Link projects.
- 7.0.2. According to the Final EM&A Report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011 and no Project-related exceedance was recorded for air and noise monitoring. It can be concluded that cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was insignificant.
- 7.0.3. According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area, removal of L-shape wall and installation of caisson seawall were performed in this reporting quarter. As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were marine works at HKCEC area, tunnel works and foundation works at Wan Chai East and temporary reclamation at Wan Chai West. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were bridge construction and road works at Central Interchange, land based bored pilling works and ELS works at Victoria Park, D- wall construction and ELS at TS3, IEC demolition and tunnel works at North Point area in this reporting quater.
- 7.0.5. No significant air impact from construction activities was anticipated in the reporting month. Besides, no project related exceedance was recorded during the air and noise environmental monitoring events in the reporting month. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) was insignificant.


8. CONCLUSION

- 8.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 8.0.2. No non-compliance was noted and no prosecution was received during the March and April reporting month.
- 8.0.3. Two limit level exceedances at M6 – HK Baptist Church Henrietta Secondary School were recorded on 5 and 27 May 2015 in May reporting month. The exceedance were concluded as related to Project works. Rectification measures was implemented by the Contractor and no further exceedances were recorded during additional monitoring.
- 8.0.4. The construction programmes of individual contracts are provided in **Appendix 8.1.**



Figure 2.1

Project Layout

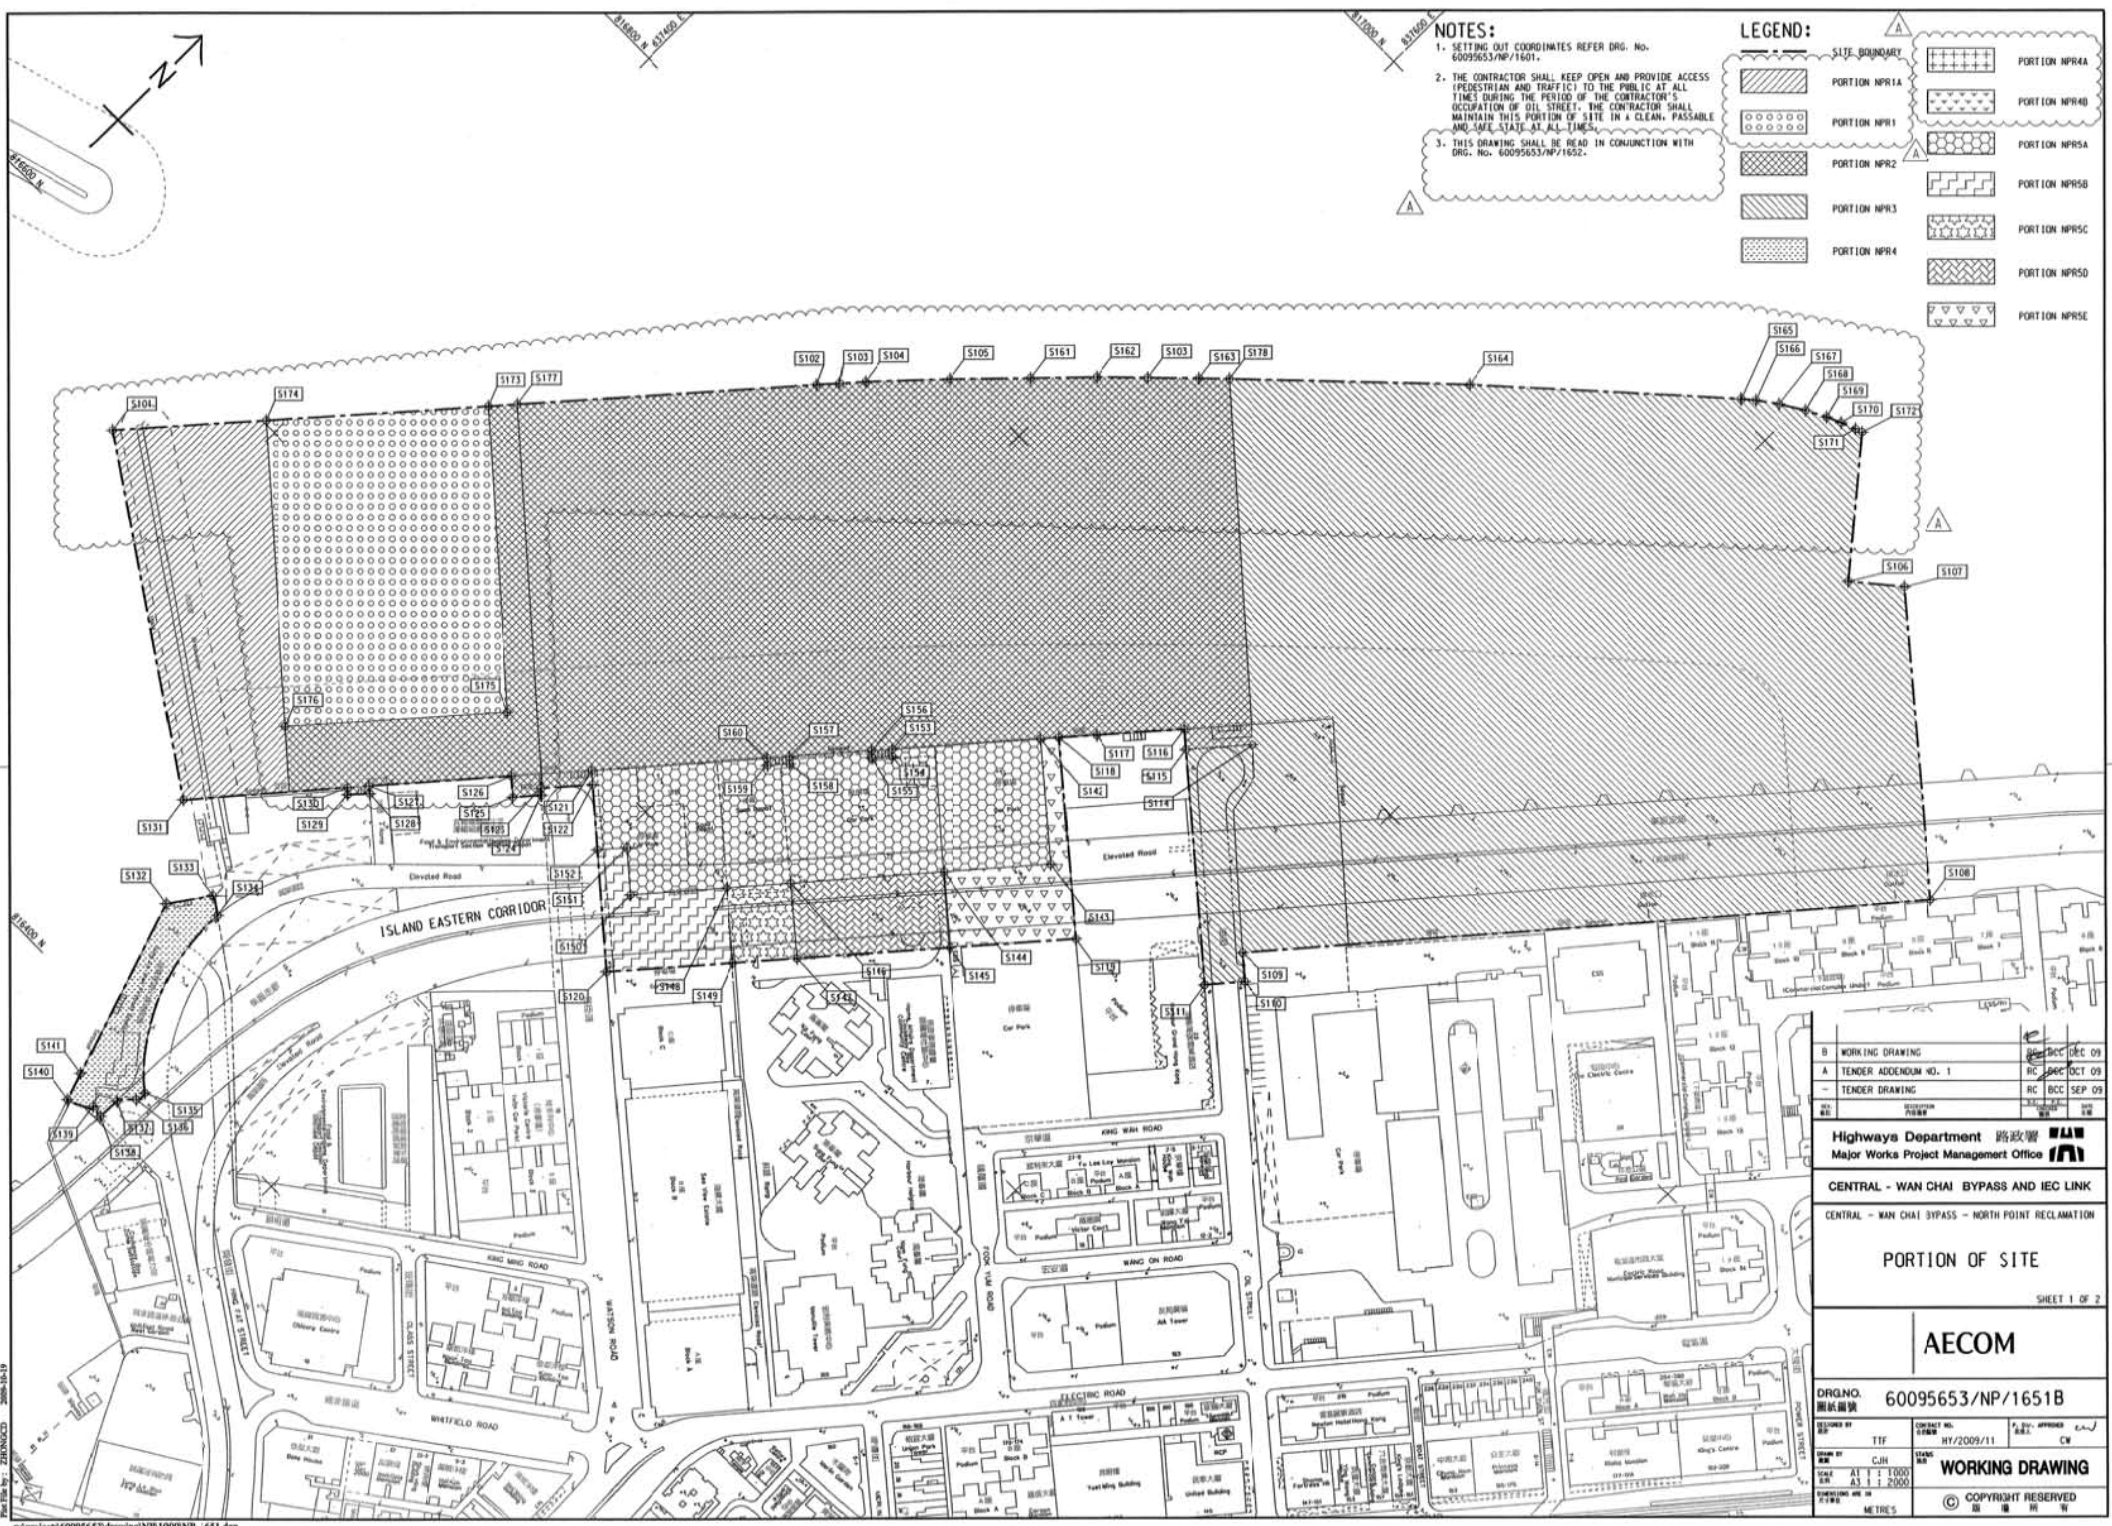

NOTES:

- 1. SETTING OUT COORDINATES REFER DRG. NO. 60095653/NP/1601.
- 2. THE CONTRACTOR SHALL KEEP OPEN AND PROVIDE ACCESS (PEDESTRIAN AND TRAFFIC) TO THE PUBLIC AT ALL TIMES DURING THE PERIOD OF THE CONTRACTOR'S OCCUPATION OF OIL STREET. THE CONTRACTOR SHALL MAINTAIN THIS PORTION OF SITE IN A CLEAN, PASSABLE AND SAFE STATE AT ALL TIMES.
- 3. THIS DRAWING SHALL BE READ IN CONJUNCTION WITH DRG. NO. 60095653/NP/1652.

LEGEND:

	SITE BOUNDARY		PORTION NPR4A
	PORTION NPR1A		PORTION NPR4B
	PORTION NPR1		PORTION NPR5A
	PORTION NPR2		PORTION NPR5B
	PORTION NPR3		PORTION NPR5C
	PORTION NPR4		PORTION NPR5D
			PORTION NPR5E

B	WORKING DRAWING	DEC 09
A	TENDER ADDENDUM NO. 1	OCT 09
	TENDER DRAWING	SEP 09



Highways Department 路政署
Major Works Project Management Office

CENTRAL - WAN CHAI BYPASS AND IEC LINK
CENTRAL - WAN CHAI BYPASS - NORTH POINT RECLAMATION

PORTION OF SITE
SHEET 1 OF 2

AECOM

DRGNO.	60095653/NP/1651B
DATE	11/11/2009
SCALE	AS SHOWN
UNIT	METRES
DESIGNED BY	TTF
CHECKED BY	CJH
DATE	11/11/2009
STATUS	WORKING DRAWING
APPROVED BY	CW
DATE	11/11/2009
REVISION	

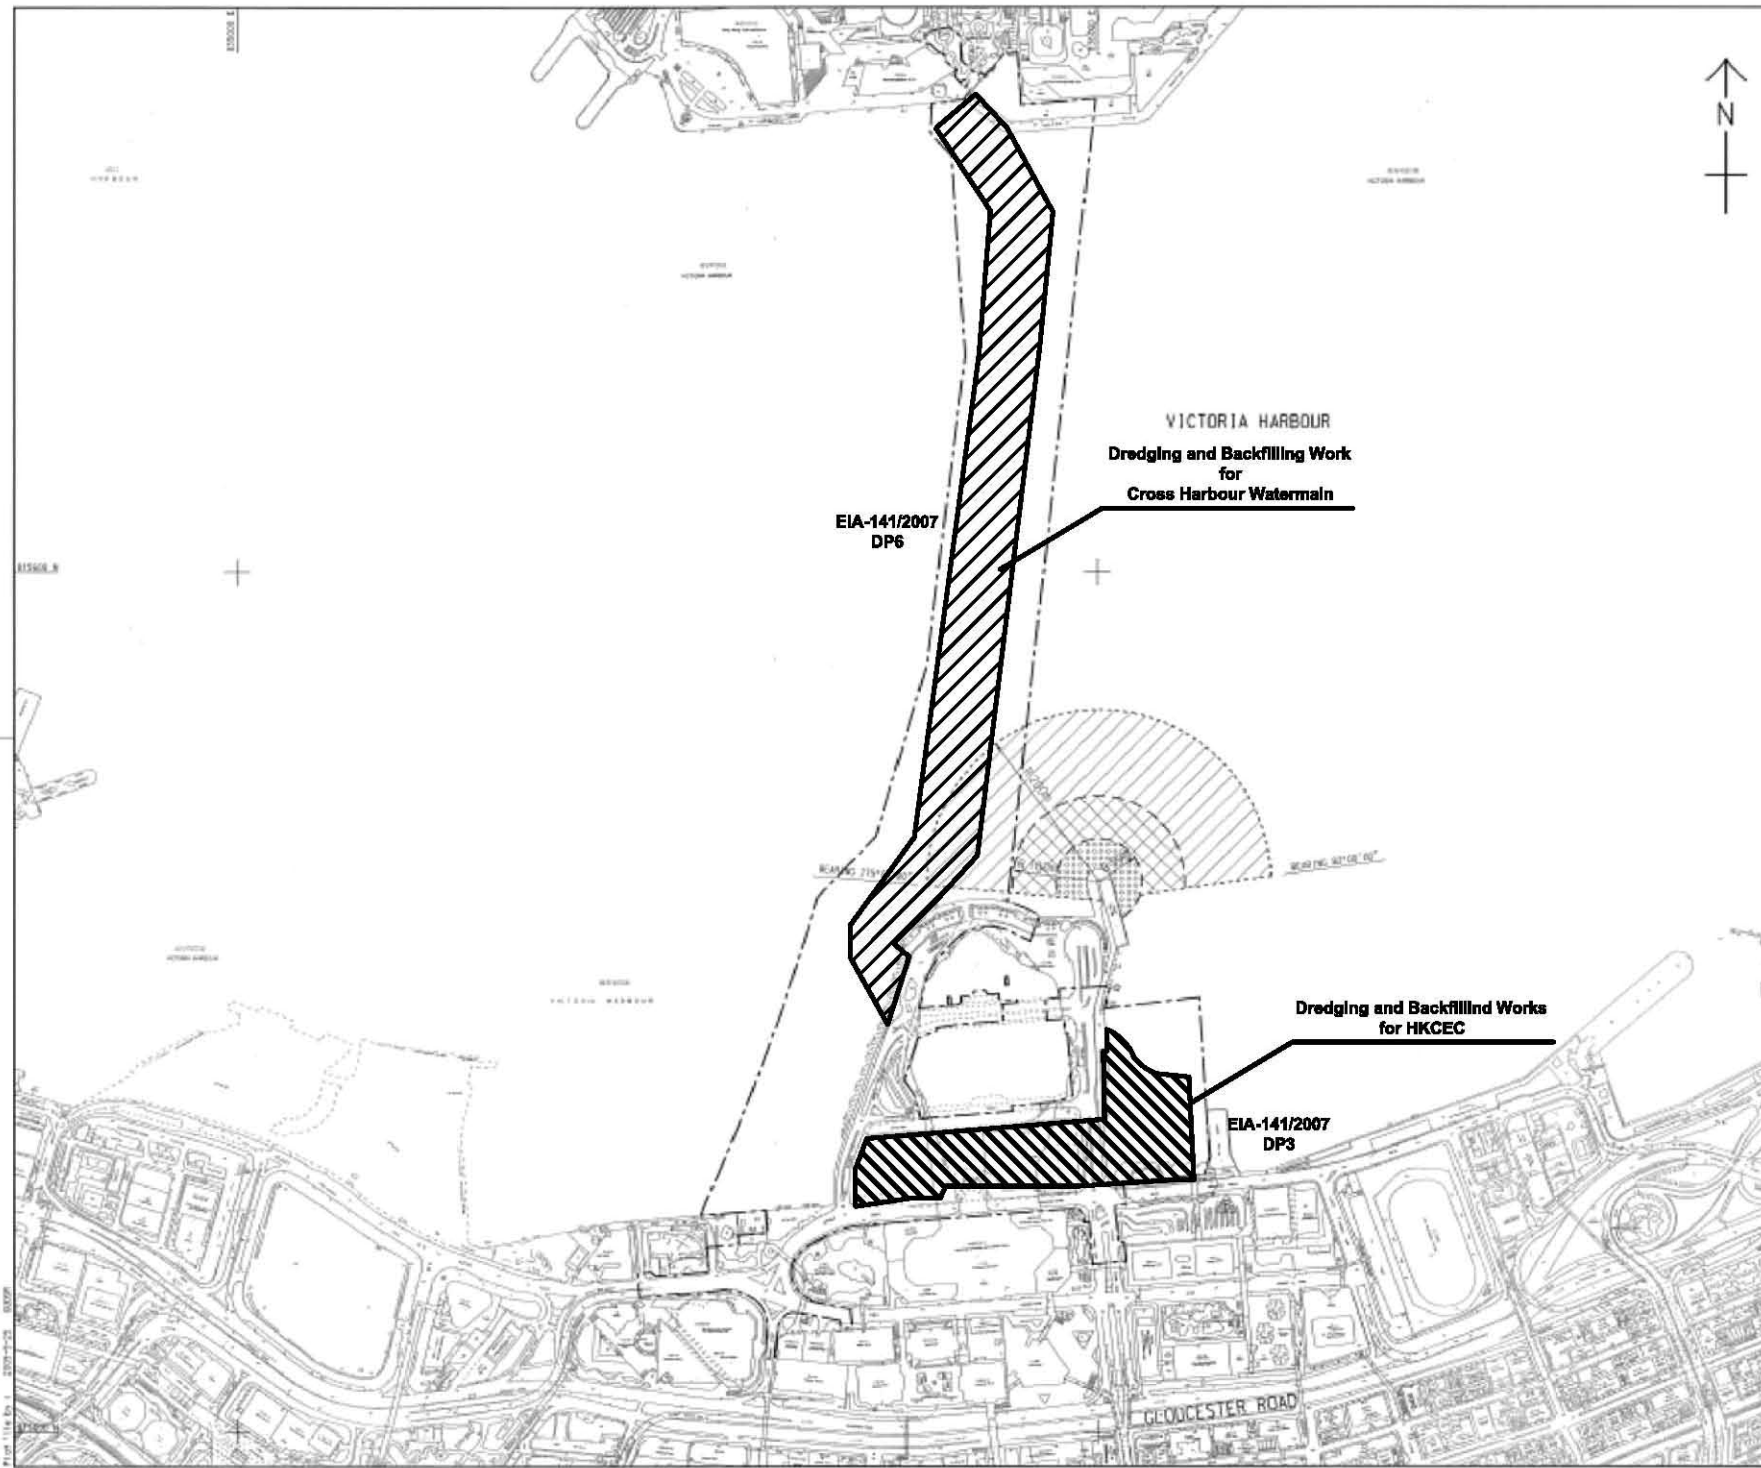

LOCATION PLAN
SCALE 1 : 5000

NOTES:

1. ALL DIMENSIONS ARE IN METRES UNLESS OTHERWISE NOTED.
2. THE RESTRICTION ZONE IS THIS DRAWING WILL COME INTO EFFECT AFTER THE OPERATION OF THE GOVERNMENT HULLING AT 10:00 DRIVE EAST.

LEGEND:

- CONTRACT BOUNDARY
- [Hatched Box] WORKING RESTRICTION ZONE
- [Cross-hatched Box] NAVIGATION AND WORKING RESTRICTION ZONE
- [Dotted Box] WORKING BARGE, NAVIGATION AND WORKING RESTRICTION ZONE

9	TENDER ADDENDUM NO. 4	10/09/09	SEP-09
8	TENDER ADDENDUM NO. 1	10/09/09	SEP-09
7	TENDER DRAWING	10/09/09	SEP-09

土木工務局
Civil Engineering and Development Department

WAN CHAI DEVELOPMENT PHASE II


WAN CHAI DEVELOPMENT PHASE II -
KONG KONG CONVERSION AND EXHIBITION CENTRE

RESTRICTED ZONE FOR
CONSTRUCTION VESSELS
(Contract no: HK/2009/01)

AECOM

DRAWING NO. 60041297/C1/100/10108

DATE	10/09/09	DATE	10/09/09
BY	ABC	BY	ABC
CHK	ABC	CHK	ABC
APP	ABC	APP	ABC
SCALE	A3 1:5000	SCALE	A3 1:5000
COPYRIGHT	RESERVED	COPYRIGHT	RESERVED

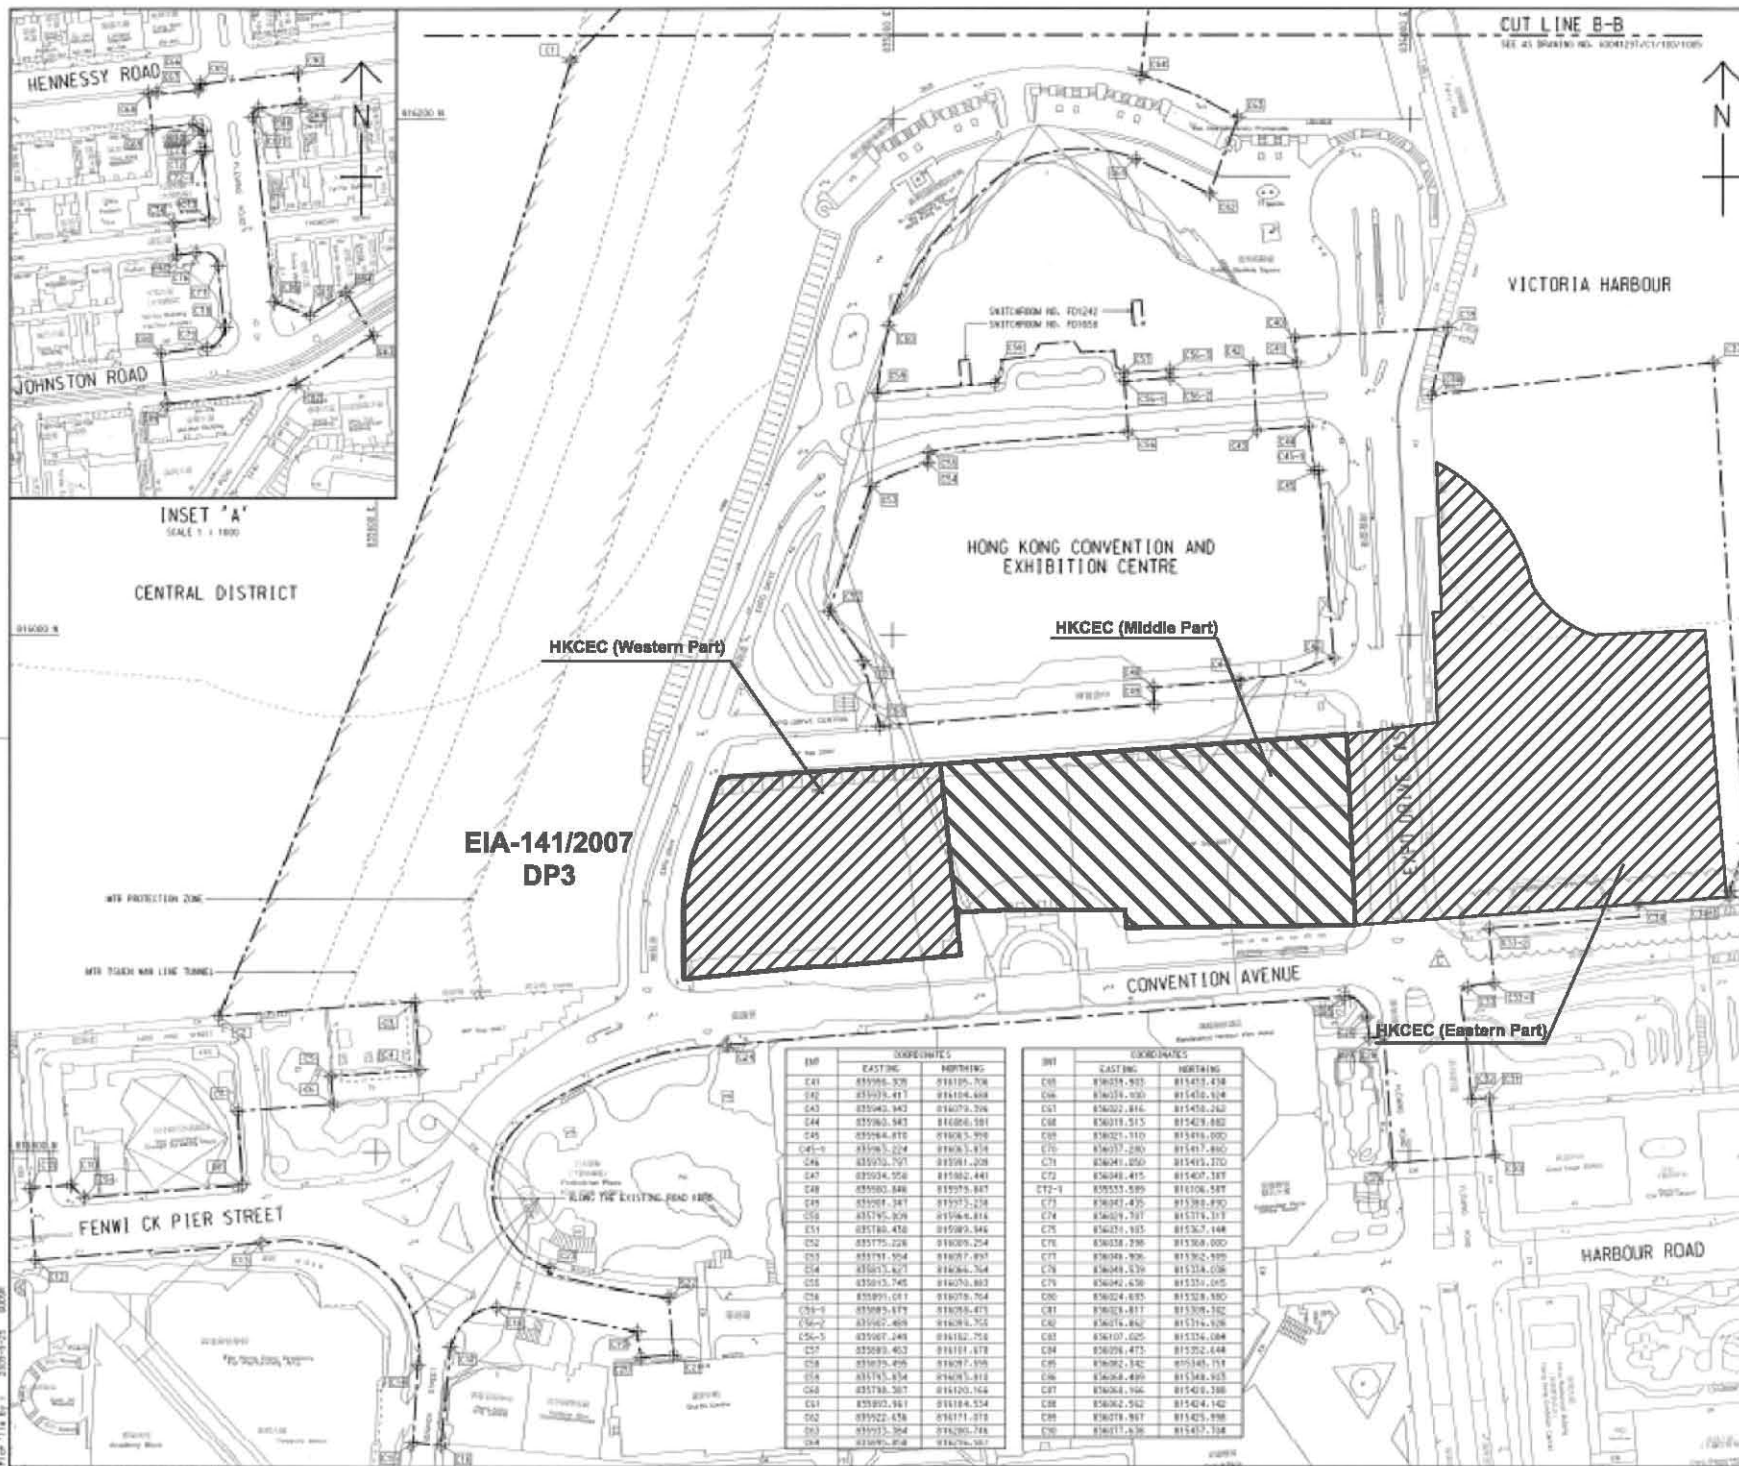

KEY PLAN
SCALE 1:10000

NOTE:

1. FOR NOTES & LEGEND, REFER TO DRAWING NO. 60041297/C1/100/1006C.

INT	COORDINATES	
	EASTING	NORTHING
C1	836875.205	816222.551
C2	836757.971	816028.595
C3	836414.365	816028.525
C4	836417.020	816031.014
C5	836582.402	816029.522
C6	836581.564	816018.612
C7	836586.565	816015.191
C8	836586.191	816011.167
C9	836486.433	816032.241
C10	836481.082	816031.056
C11	836485.769	816038.075
C12	836467.486	816038.027
C13	836555.460	816044.817
C14	836486.433	816077.122
C15	836414.365	816086.593
C16	836425.195	816085.525
C17	836429.730	816074.447
C18	836446.085	816078.816
C19	836781.421	816050.587
C20	836702.537	816020.895
C21	836711.295	816021.484
C22	836713.183	816023.452
C23	836627.096	816009.074
C24	836735.964	816003.670
C25	836715.280	816000.251
C26	836801.667	816012.286
C27	836804.075	816043.836
C28	836796.218	816044.545
C29	836951.523	816076.385
C30	836933.781	816058.637
C31	836931.216	816028.470
C32	836824.182	816025.117
C33	836821.081	816015.582
C34	836826.795	816004.705
C35	836827.425	816003.286
C36	836809.151	816003.286
C37	836824.032	816004.095
C38	836824.047	816003.286
C39	836826.850	816019.734
C40	836819.190	816026.057
C41	836826.810	816023.295
C42	836816.985	816019.080
C43	836825.682	816015.582

C	TENDER ADDENDUM NO.4	SHEN YU SEP 08
E	TENDER ADDENDUM NO.2	SHEN YU SEP 08
A	TENDER ADDENDUM NO.1	SHEN YU SEP 08
-	TENDER DRAWING	SHEN YU SEP 08
W	WATER	SHEN YU SEP 08

土木工程發展局
Civil Engineering and Development Department

WAN CHAI DEVELOPMENT PHASE II


WAN CHAI DEVELOPMENT PHASE II -
CONTRACT NO. HK/2009/01
HONG KONG CONVENTION AND EXHIBITION CENTRE

SITE BOUNDARY
SETTING OUT PLAN
(Contract no. HK/2009/01)

AECOM

DRAWING NO. 60041297/C1/100/1006C

DATE	REV	BY	CHKD	APPD
11/11/2008	1	WJ	WJ	WJ
11/11/2008	2	WJ	WJ	WJ
11/11/2008	3	WJ	WJ	WJ
11/11/2008	4	WJ	WJ	WJ
11/11/2008	5	WJ	WJ	WJ
11/11/2008	6	WJ	WJ	WJ
11/11/2008	7	WJ	WJ	WJ
11/11/2008	8	WJ	WJ	WJ
11/11/2008	9	WJ	WJ	WJ
11/11/2008	10	WJ	WJ	WJ
11/11/2008	11	WJ	WJ	WJ
11/11/2008	12	WJ	WJ	WJ
11/11/2008	13	WJ	WJ	WJ
11/11/2008	14	WJ	WJ	WJ
11/11/2008	15	WJ	WJ	WJ
11/11/2008	16	WJ	WJ	WJ
11/11/2008	17	WJ	WJ	WJ
11/11/2008	18	WJ	WJ	WJ
11/11/2008	19	WJ	WJ	WJ
11/11/2008	20	WJ	WJ	WJ
11/11/2008	21	WJ	WJ	WJ
11/11/2008	22	WJ	WJ	WJ
11/11/2008	23	WJ	WJ	WJ
11/11/2008	24	WJ	WJ	WJ
11/11/2008	25	WJ	WJ	WJ
11/11/2008	26	WJ	WJ	WJ
11/11/2008	27	WJ	WJ	WJ
11/11/2008	28	WJ	WJ	WJ
11/11/2008	29	WJ	WJ	WJ
11/11/2008	30	WJ	WJ	WJ
11/11/2008	31	WJ	WJ	WJ
11/11/2008	32	WJ	WJ	WJ
11/11/2008	33	WJ	WJ	WJ
11/11/2008	34	WJ	WJ	WJ
11/11/2008	35	WJ	WJ	WJ
11/11/2008	36	WJ	WJ	WJ
11/11/2008	37	WJ	WJ	WJ
11/11/2008	38	WJ	WJ	WJ
11/11/2008	39	WJ	WJ	WJ
11/11/2008	40	WJ	WJ	WJ
11/11/2008	41	WJ	WJ	WJ
11/11/2008	42	WJ	WJ	WJ
11/11/2008	43	WJ	WJ	WJ
11/11/2008	44	WJ	WJ	WJ
11/11/2008	45	WJ	WJ	WJ
11/11/2008	46	WJ	WJ	WJ
11/11/2008	47	WJ	WJ	WJ
11/11/2008	48	WJ	WJ	WJ
11/11/2008	49	WJ	WJ	WJ
11/11/2008	50	WJ	WJ	WJ
11/11/2008	51	WJ	WJ	WJ
11/11/2008	52	WJ	WJ	WJ
11/11/2008	53	WJ	WJ	WJ
11/11/2008	54	WJ	WJ	WJ
11/11/2008	55	WJ	WJ	WJ
11/11/2008	56	WJ	WJ	WJ
11/11/2008	57	WJ	WJ	WJ
11/11/2008	58	WJ	WJ	WJ
11/11/2008	59	WJ	WJ	WJ
11/11/2008	60	WJ	WJ	WJ
11/11/2008	61	WJ	WJ	WJ
11/11/2008	62	WJ	WJ	WJ
11/11/2008	63	WJ	WJ	WJ
11/11/2008	64	WJ	WJ	WJ
11/11/2008	65	WJ	WJ	WJ
11/11/2008	66	WJ	WJ	WJ
11/11/2008	67	WJ	WJ	WJ
11/11/2008	68	WJ	WJ	WJ
11/11/2008	69	WJ	WJ	WJ
11/11/2008	70	WJ	WJ	WJ
11/11/2008	71	WJ	WJ	WJ
11/11/2008	72	WJ	WJ	WJ
11/11/2008	73	WJ	WJ	WJ
11/11/2008	74	WJ	WJ	WJ
11/11/2008	75	WJ	WJ	WJ
11/11/2008	76	WJ	WJ	WJ
11/11/2008	77	WJ	WJ	WJ
11/11/2008	78	WJ	WJ	WJ
11/11/2008	79	WJ	WJ	WJ
11/11/2008	80	WJ	WJ	WJ
11/11/2008	81	WJ	WJ	WJ
11/11/2008	82	WJ	WJ	WJ
11/11/2008	83	WJ	WJ	WJ
11/11/2008	84	WJ	WJ	WJ
11/11/2008	85	WJ	WJ	WJ
11/11/2008	86	WJ	WJ	WJ
11/11/2008	87	WJ	WJ	WJ
11/11/2008	88	WJ	WJ	WJ
11/11/2008	89	WJ	WJ	WJ
11/11/2008	90	WJ	WJ	WJ
11/11/2008	91	WJ	WJ	WJ
11/11/2008	92	WJ	WJ	WJ
11/11/2008	93	WJ	WJ	WJ
11/11/2008	94	WJ	WJ	WJ
11/11/2008	95	WJ	WJ	WJ
11/11/2008	96	WJ	WJ	WJ
11/11/2008	97	WJ	WJ	WJ
11/11/2008	98	WJ	WJ	WJ
11/11/2008	99	WJ	WJ	WJ
11/11/2008	100	WJ	WJ	WJ

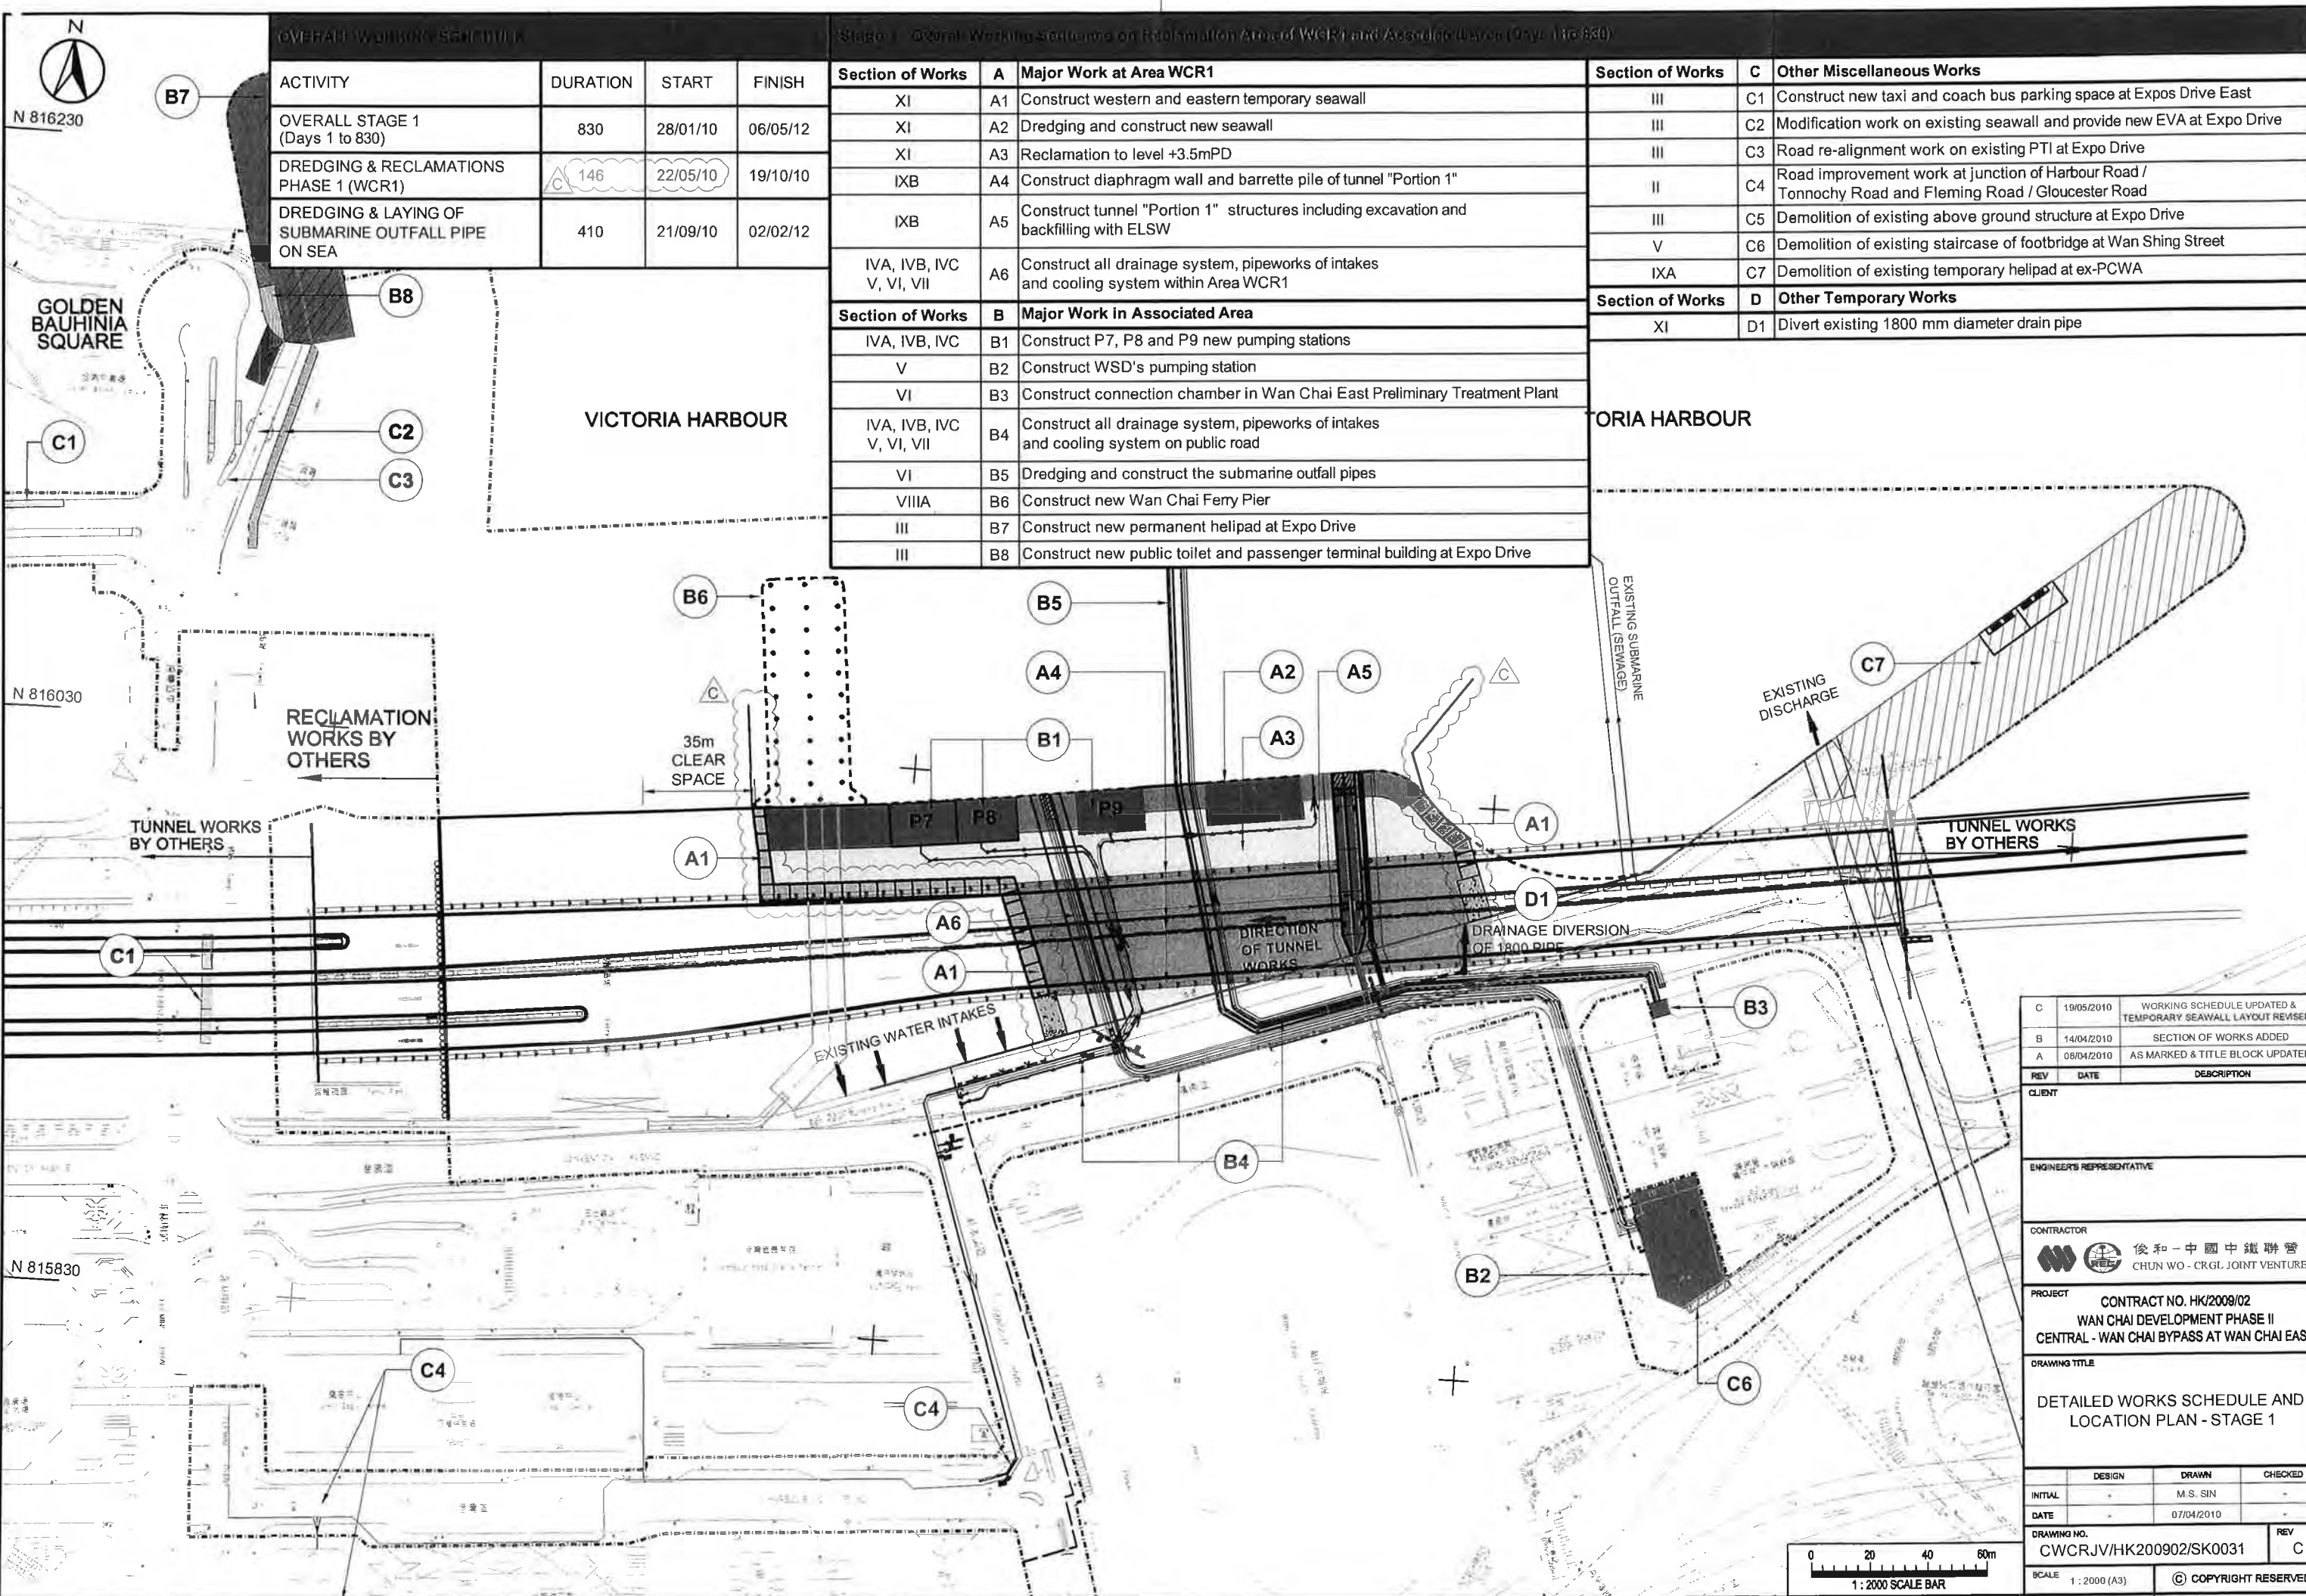

OVERALL WORKING SCHEDULE			
ACTIVITY	DURATION	START	FINISH
OVERALL STAGE 1 (Days 1 to 830)	830	28/01/10	06/05/12
DREDGING & RECLAMATIONS PHASE 1 (WCR1)	146	22/05/10	19/10/10
DREDGING & LAYING OF SUBMARINE OUTFALL PIPE ON SEA	410	21/09/10	02/02/12

Stage 1 - Overall Working Sequence on Reclamation Area of WCR1 and Associated Area (Days 1 to 830)		
Section of Works	A	Major Work at Area WCR1
XI	A1	Construct western and eastern temporary seawall
XI	A2	Dredging and construct new seawall
XI	A3	Reclamation to level +3.5mPD
IXB	A4	Construct diaphragm wall and barrette pile of tunnel "Portion 1"
IXB	A5	Construct tunnel "Portion 1" structures including excavation and backfilling with ELSW
IVA, IVB, IVC V, VI, VII	A6	Construct all drainage system, pipeworks of intakes and cooling system within Area WCR1
Section of Works	B	Major Work in Associated Area
IVA, IVB, IVC	B1	Construct P7, P8 and P9 new pumping stations
V	B2	Construct WSD's pumping station
VI	B3	Construct connection chamber in Wan Chai East Preliminary Treatment Plant
IVA, IVB, IVC V, VI, VII	B4	Construct all drainage system, pipeworks of intakes and cooling system on public road
VI	B5	Dredging and construct the submarine outfall pipes
VIIIA	B6	Construct new Wan Chai Ferry Pier
III	B7	Construct new permanent helipad at Expo Drive
III	B8	Construct new public toilet and passenger terminal building at Expo Drive

Section of Works	C	Other Miscellaneous Works
III	C1	Construct new taxi and coach bus parking space at Expos Drive East
III	C2	Modification work on existing seawall and provide new EVA at Expo Drive
III	C3	Road re-alignment work on existing PTI at Expo Drive
II	C4	Road improvement work at junction of Harbour Road / Tonnochy Road and Fleming Road / Gloucester Road
III	C5	Demolition of existing above ground structure at Expo Drive
V	C6	Demolition of existing staircase of footbridge at Wan Shing Street
IXA	C7	Demolition of existing temporary heliport at ex-PCWA
Section of Works	D	Other Temporary Works
XI	D1	Divert existing 1800 mm diameter drain pipe



C	19/05/2010	WORKING SCHEDULE UPDATED & TEMPORARY SEAWALL LAYOUT REVISED
B	14/04/2010	SECTION OF WORKS ADDED
A	08/04/2010	AS MARKED & TITLE BLOCK UPDATED
REV	DATE	DESCRIPTION
CLIENT		
ENGINEER'S REPRESENTATIVE		
CONTRACTOR		
PROJECT		
DRAWING TITLE		
DESIGN		
DRAWN		
CHECKED		
DATE		
DRAWING NO.		
SCALE		
COPYRIGHT RESERVED		

圖例：
LEGEND:

- 地界範圍
SITE BOUNDARY
- ▨ 園林綠化平台
LANDSCAPED DECK
- 主幹道隧道
TRUNK ROAD TUNNEL
- 擬建高架道路
PROPOSED ELEVATED CARRIAGEWAY
- 現有高架行車道將予拆卸
EXISTING ELEVATED CARRIAGEWAY TO BE DEMOLISHED
- 現有高架行車道將予拆卸及重建
EXISTING ELEVATED CARRIAGEWAY TO BE DEMOLISHED AND RECONSTRUCTED



維多利亞海港 ×
VICTORIA HARBOUR

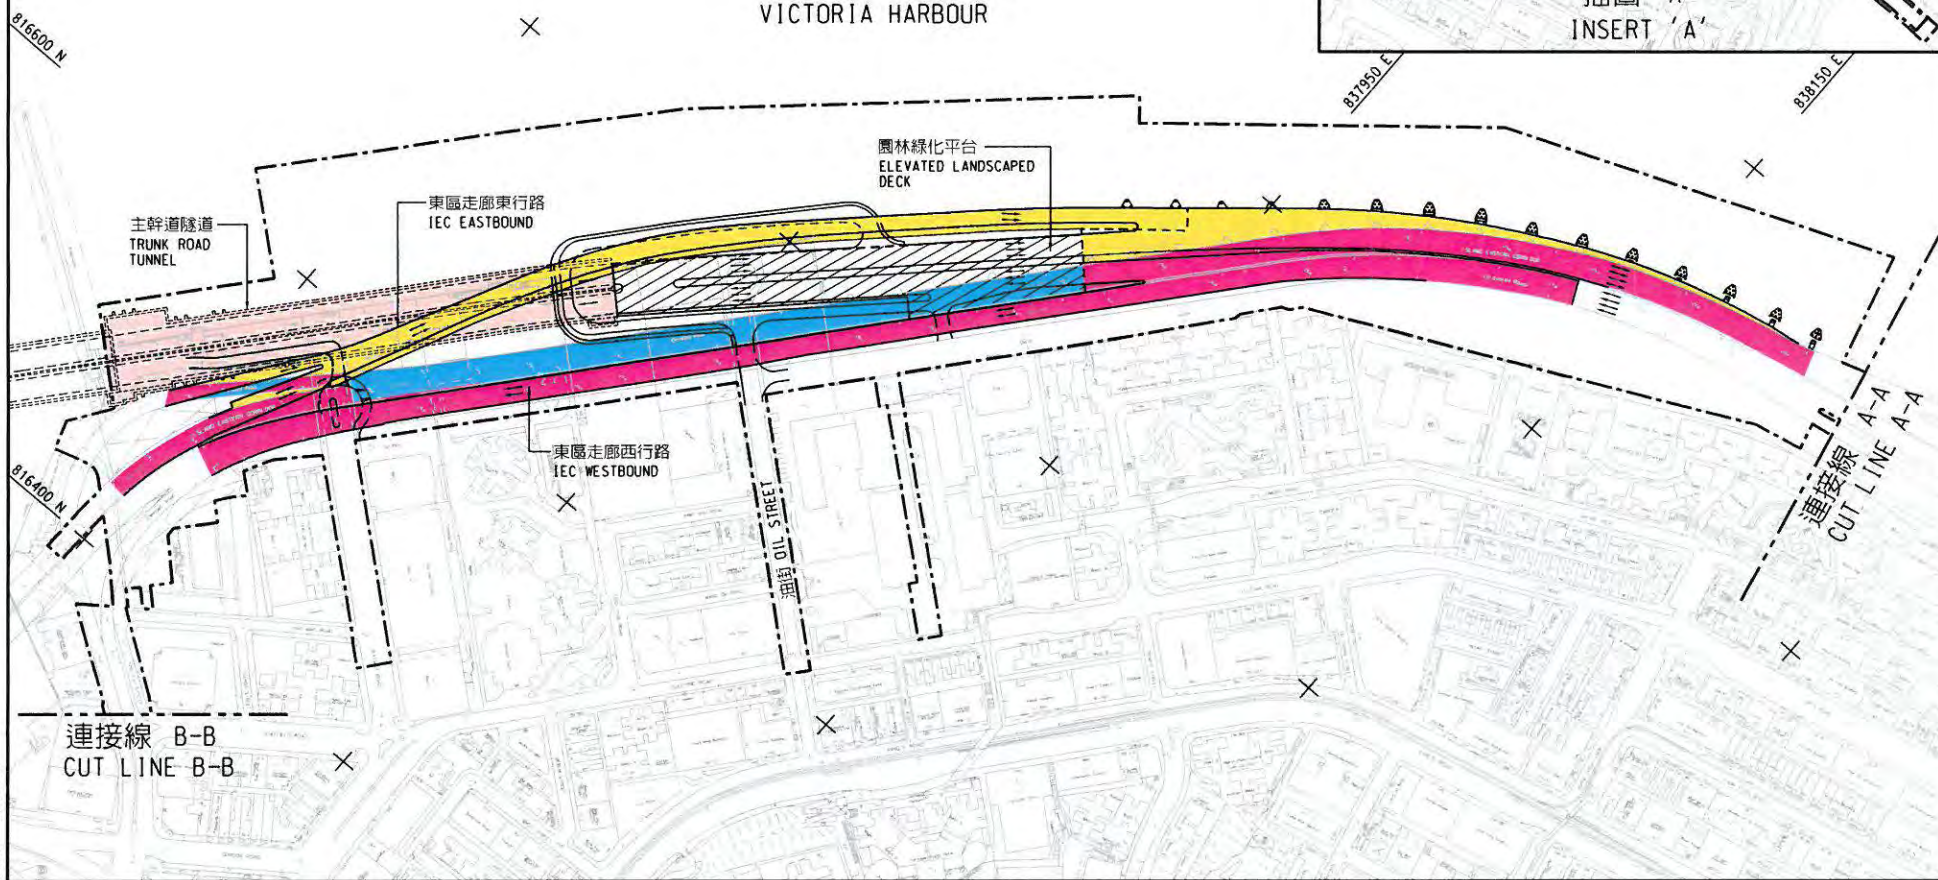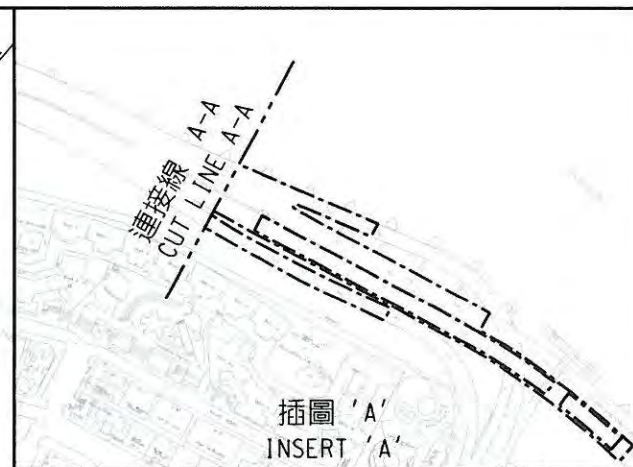

合約編號 HY/2009/19 - 中環灣仔繞道 - 北角段隧道及東區走廊連接路

CONTRACT NO. HY/2009/19 - CENTRAL-WAN CHAI BYPASS - TUNNEL (NORTH POINT SECTION) AND ISLAND EASTERN CORRIDOR LINK

SCALE 1 : 3000

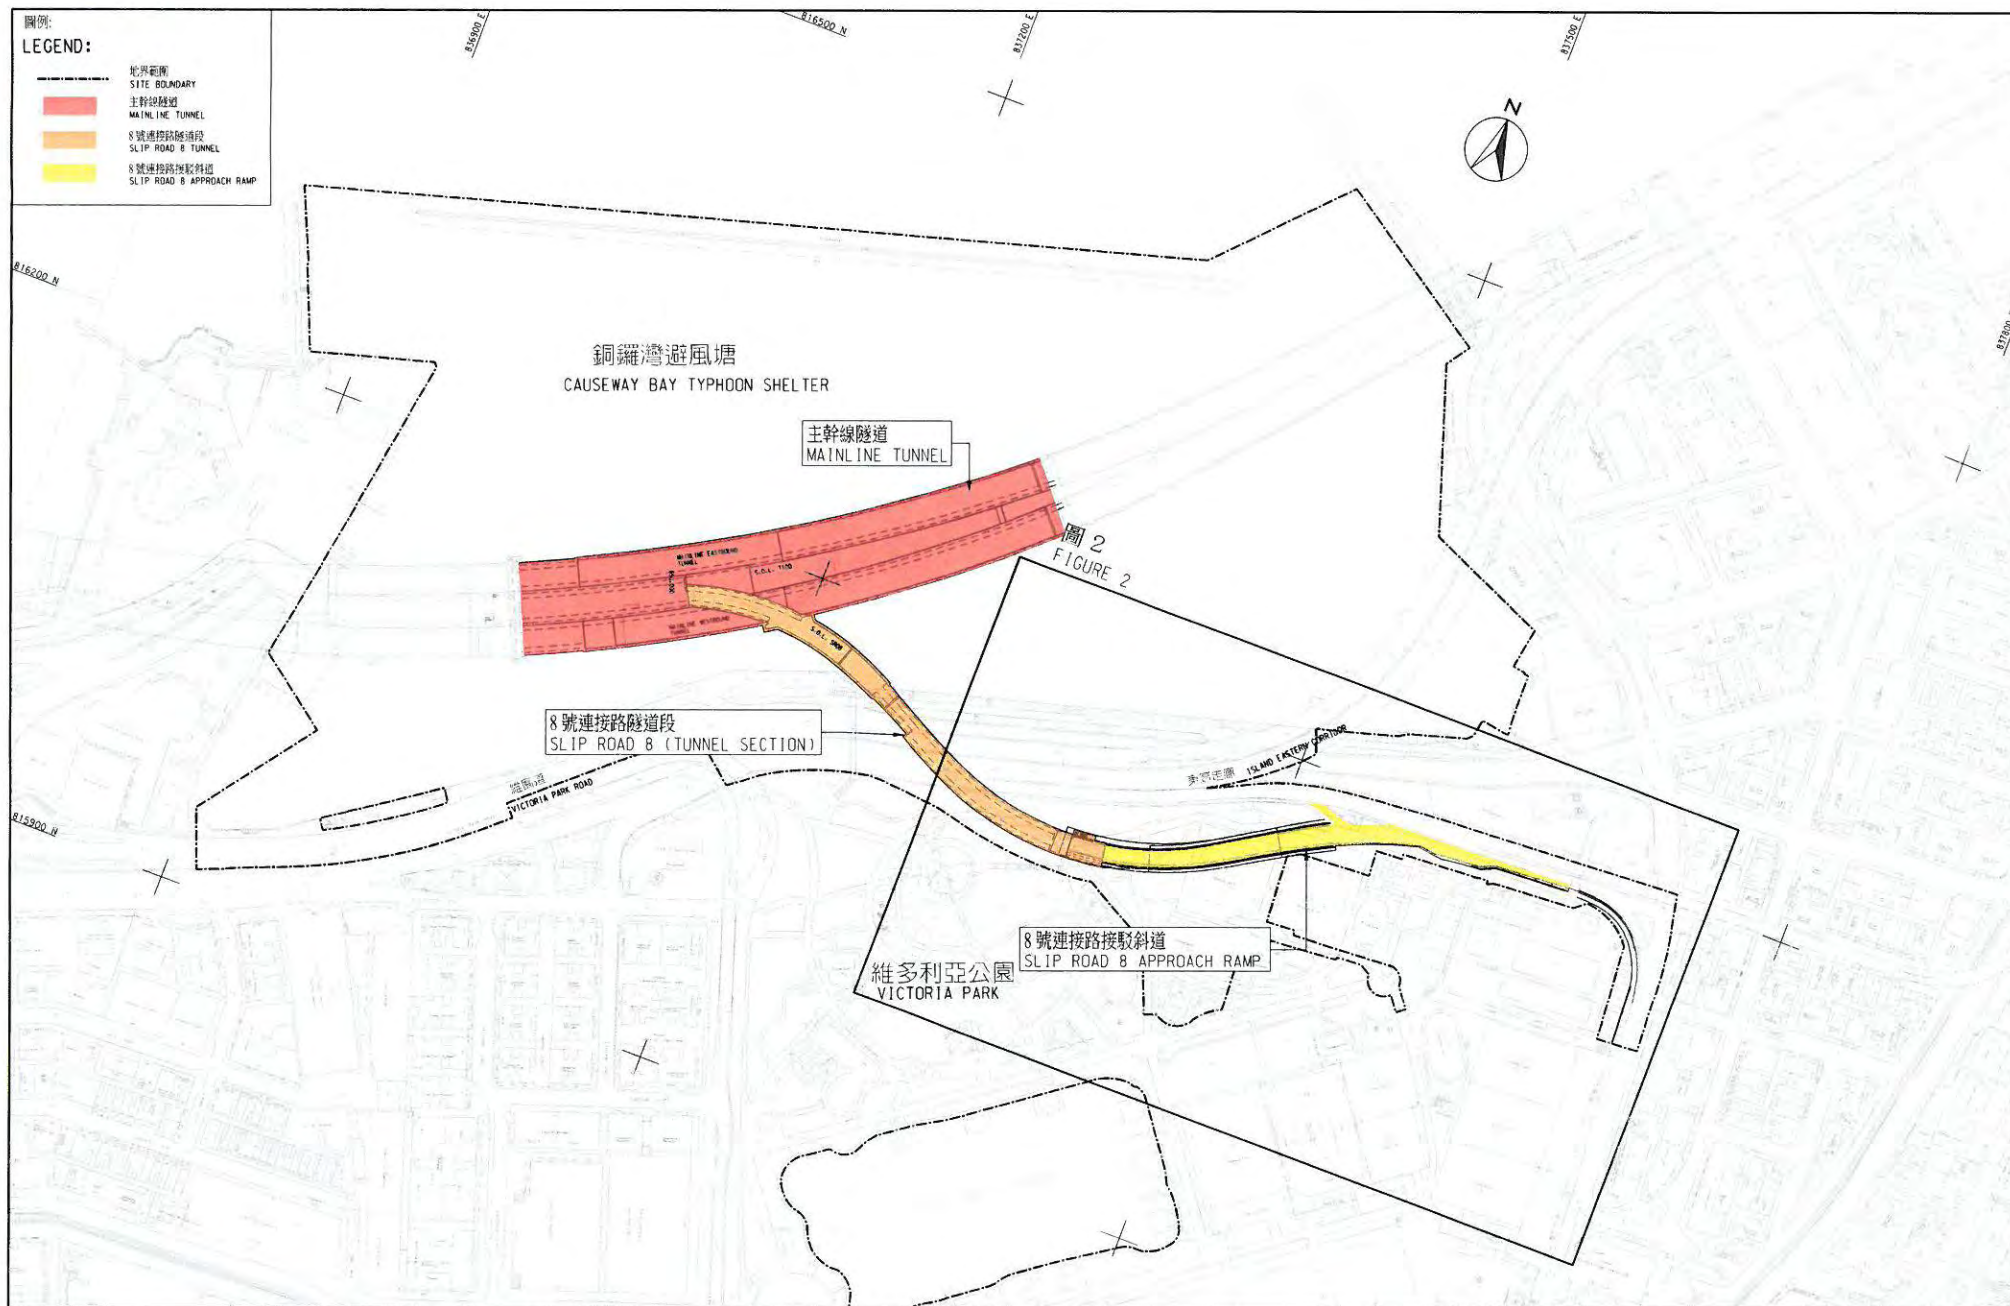


圖1- 合約編號 HY/2010/08中環灣仔繞道-8號連接路段隧道

FIGURE 1 - CONTRACT NO. HY/2010/08 - CENTRAL - WAN CHAI BYPASS - TUNNEL (SLIP ROAD 8 SECTION)

SCALE 1 : 3000

LEGEND:

WORKS AREA



WORKS AREA

DREDGING AREA FOR
MITIGATION OF ODOUR(DP3)

SITE BOUNDARY

SITE BOUNDARY

港口
HONG KONG PORT



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

Highways Department
CONTRACT NO. HY/2009/15
CENTRAL-WAN CHAI BYPASS - TUNNEL
(CAUSEWAY BAY TYPHOON
SHELTER SECTION)

TITLE
LOCATION PLAN OF WORKS AREA

DWG. NO.
CWBT/EPD/001B

SCALE
1:1000 @ A0
DIMENSIONS ARE IN
MILLIMETERS

COPYRIGHT RESERVED



Figure 2.2

Project Organization Chart



Project Organization Chart



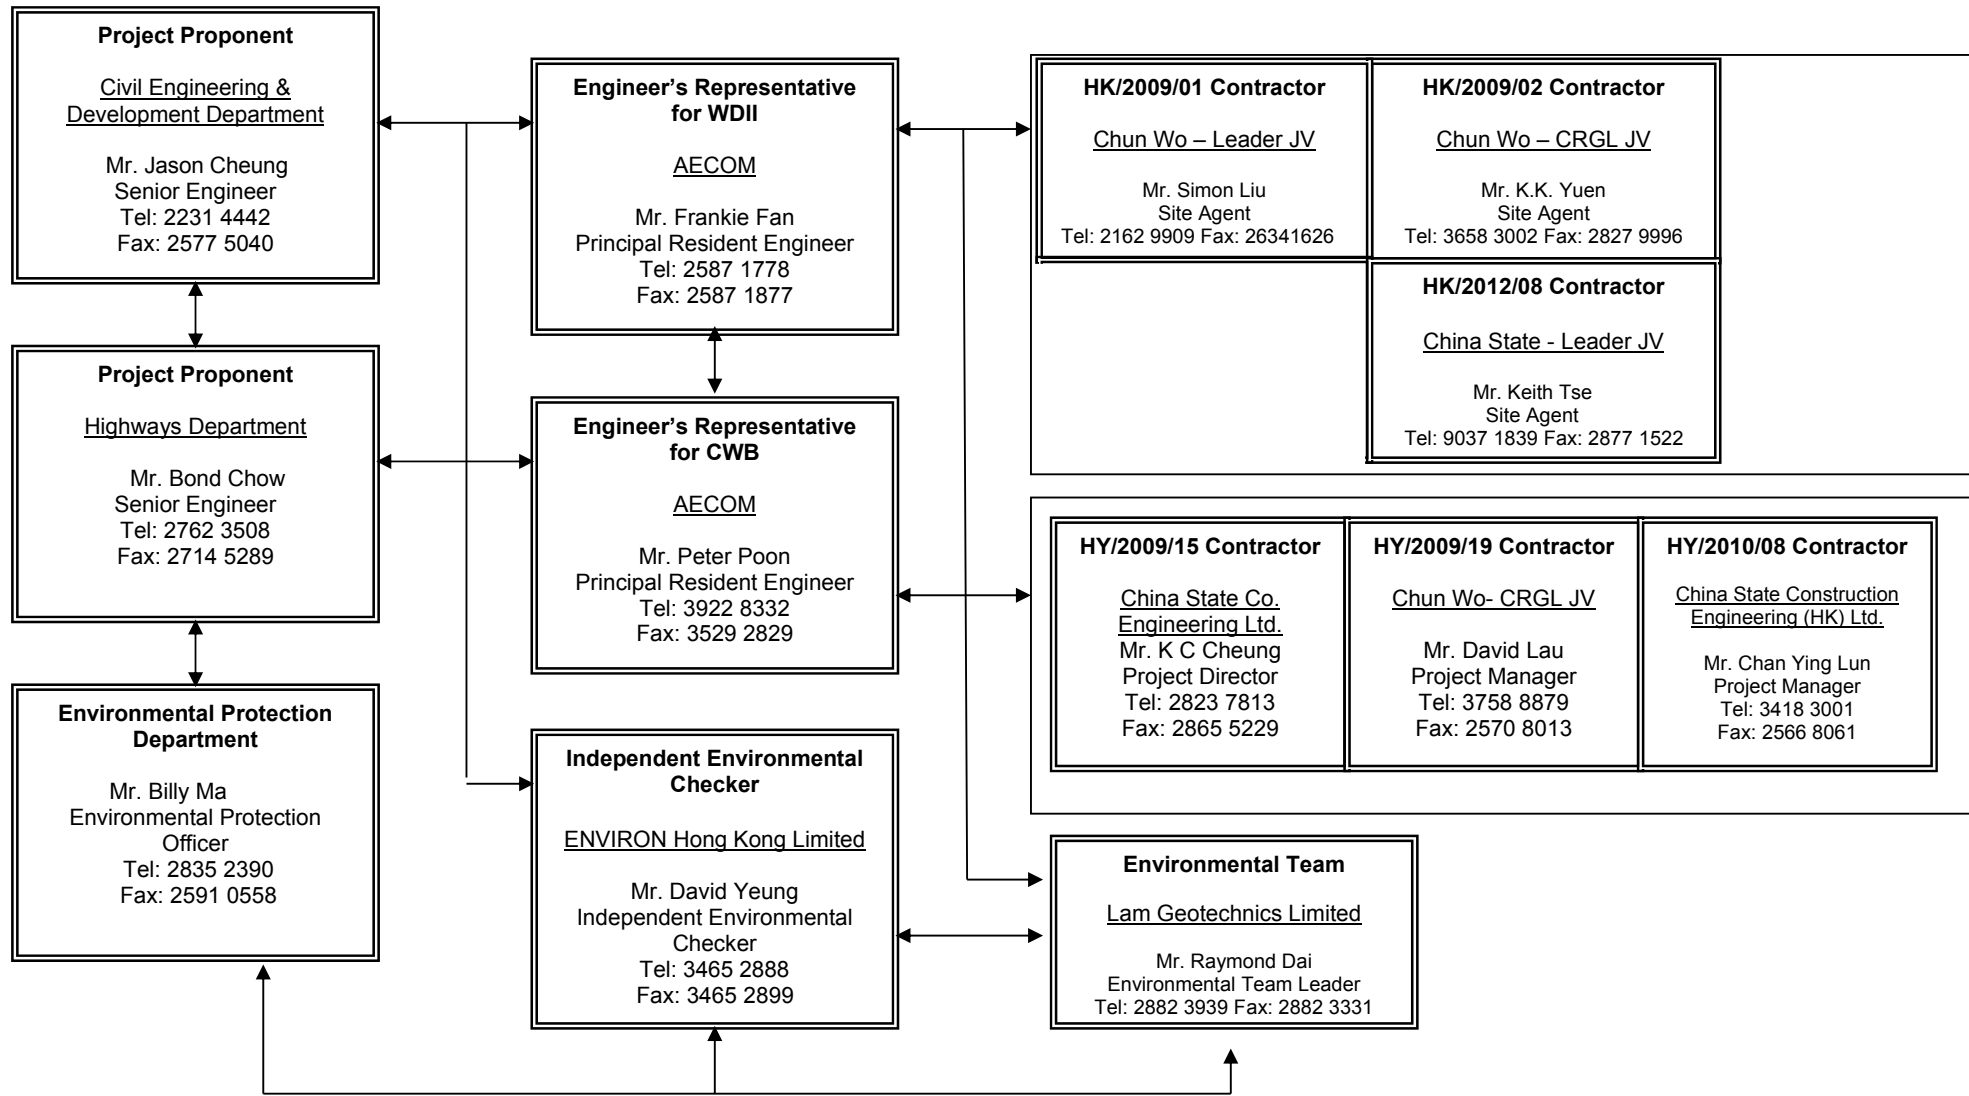




Figure 4.1

Locations of Monitoring Stations

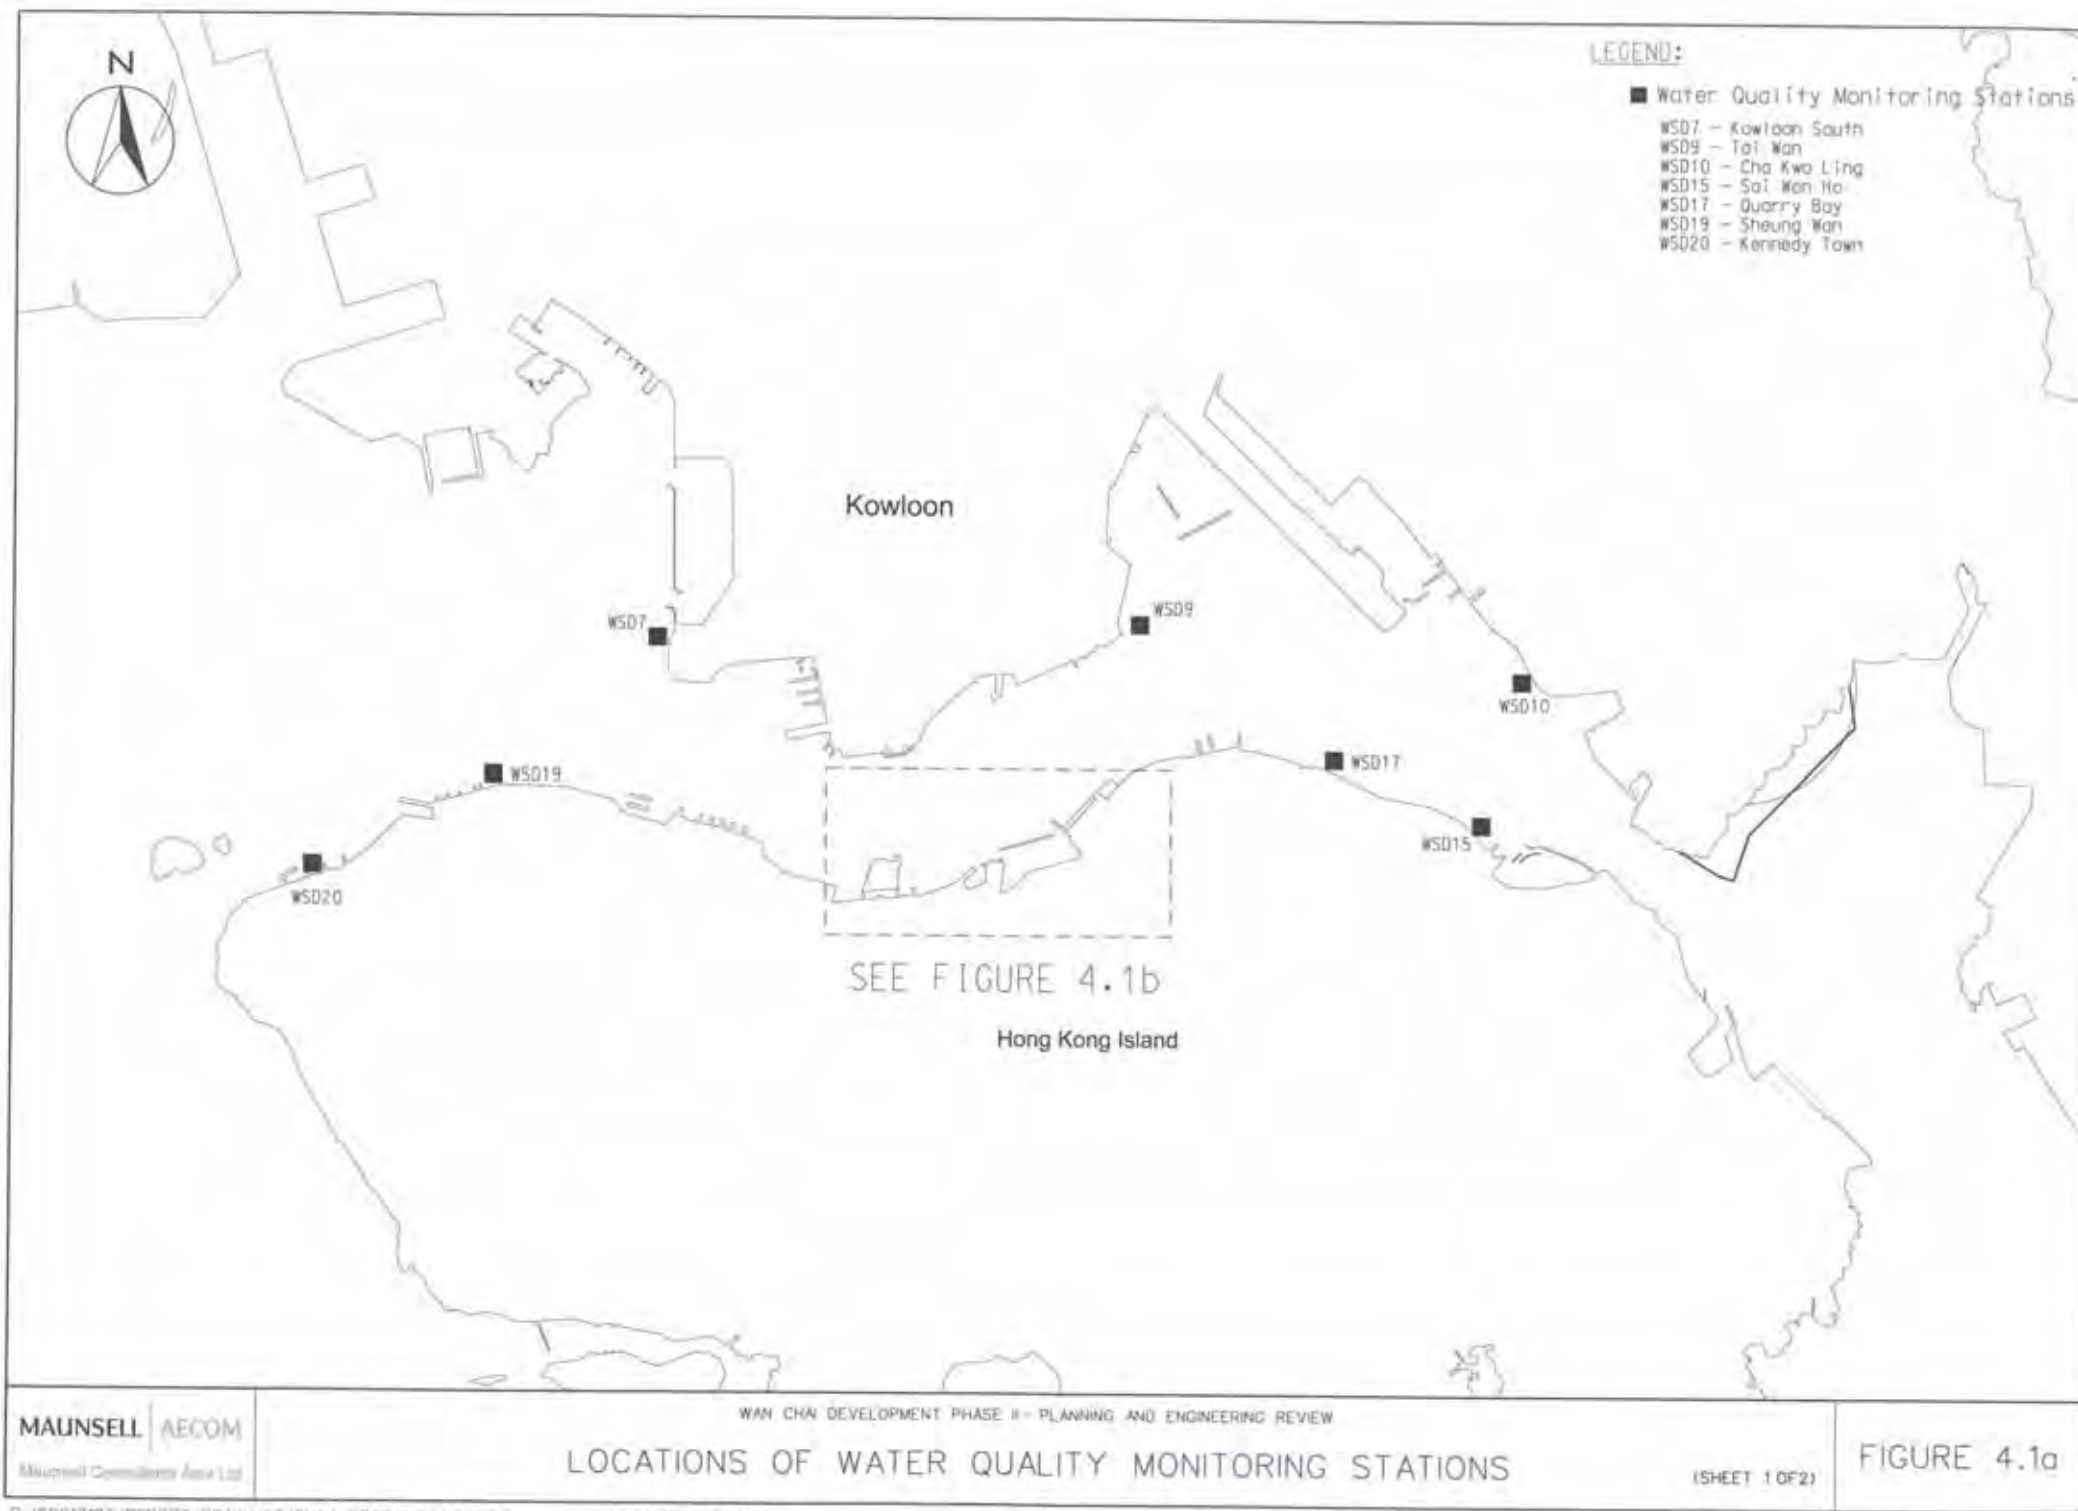


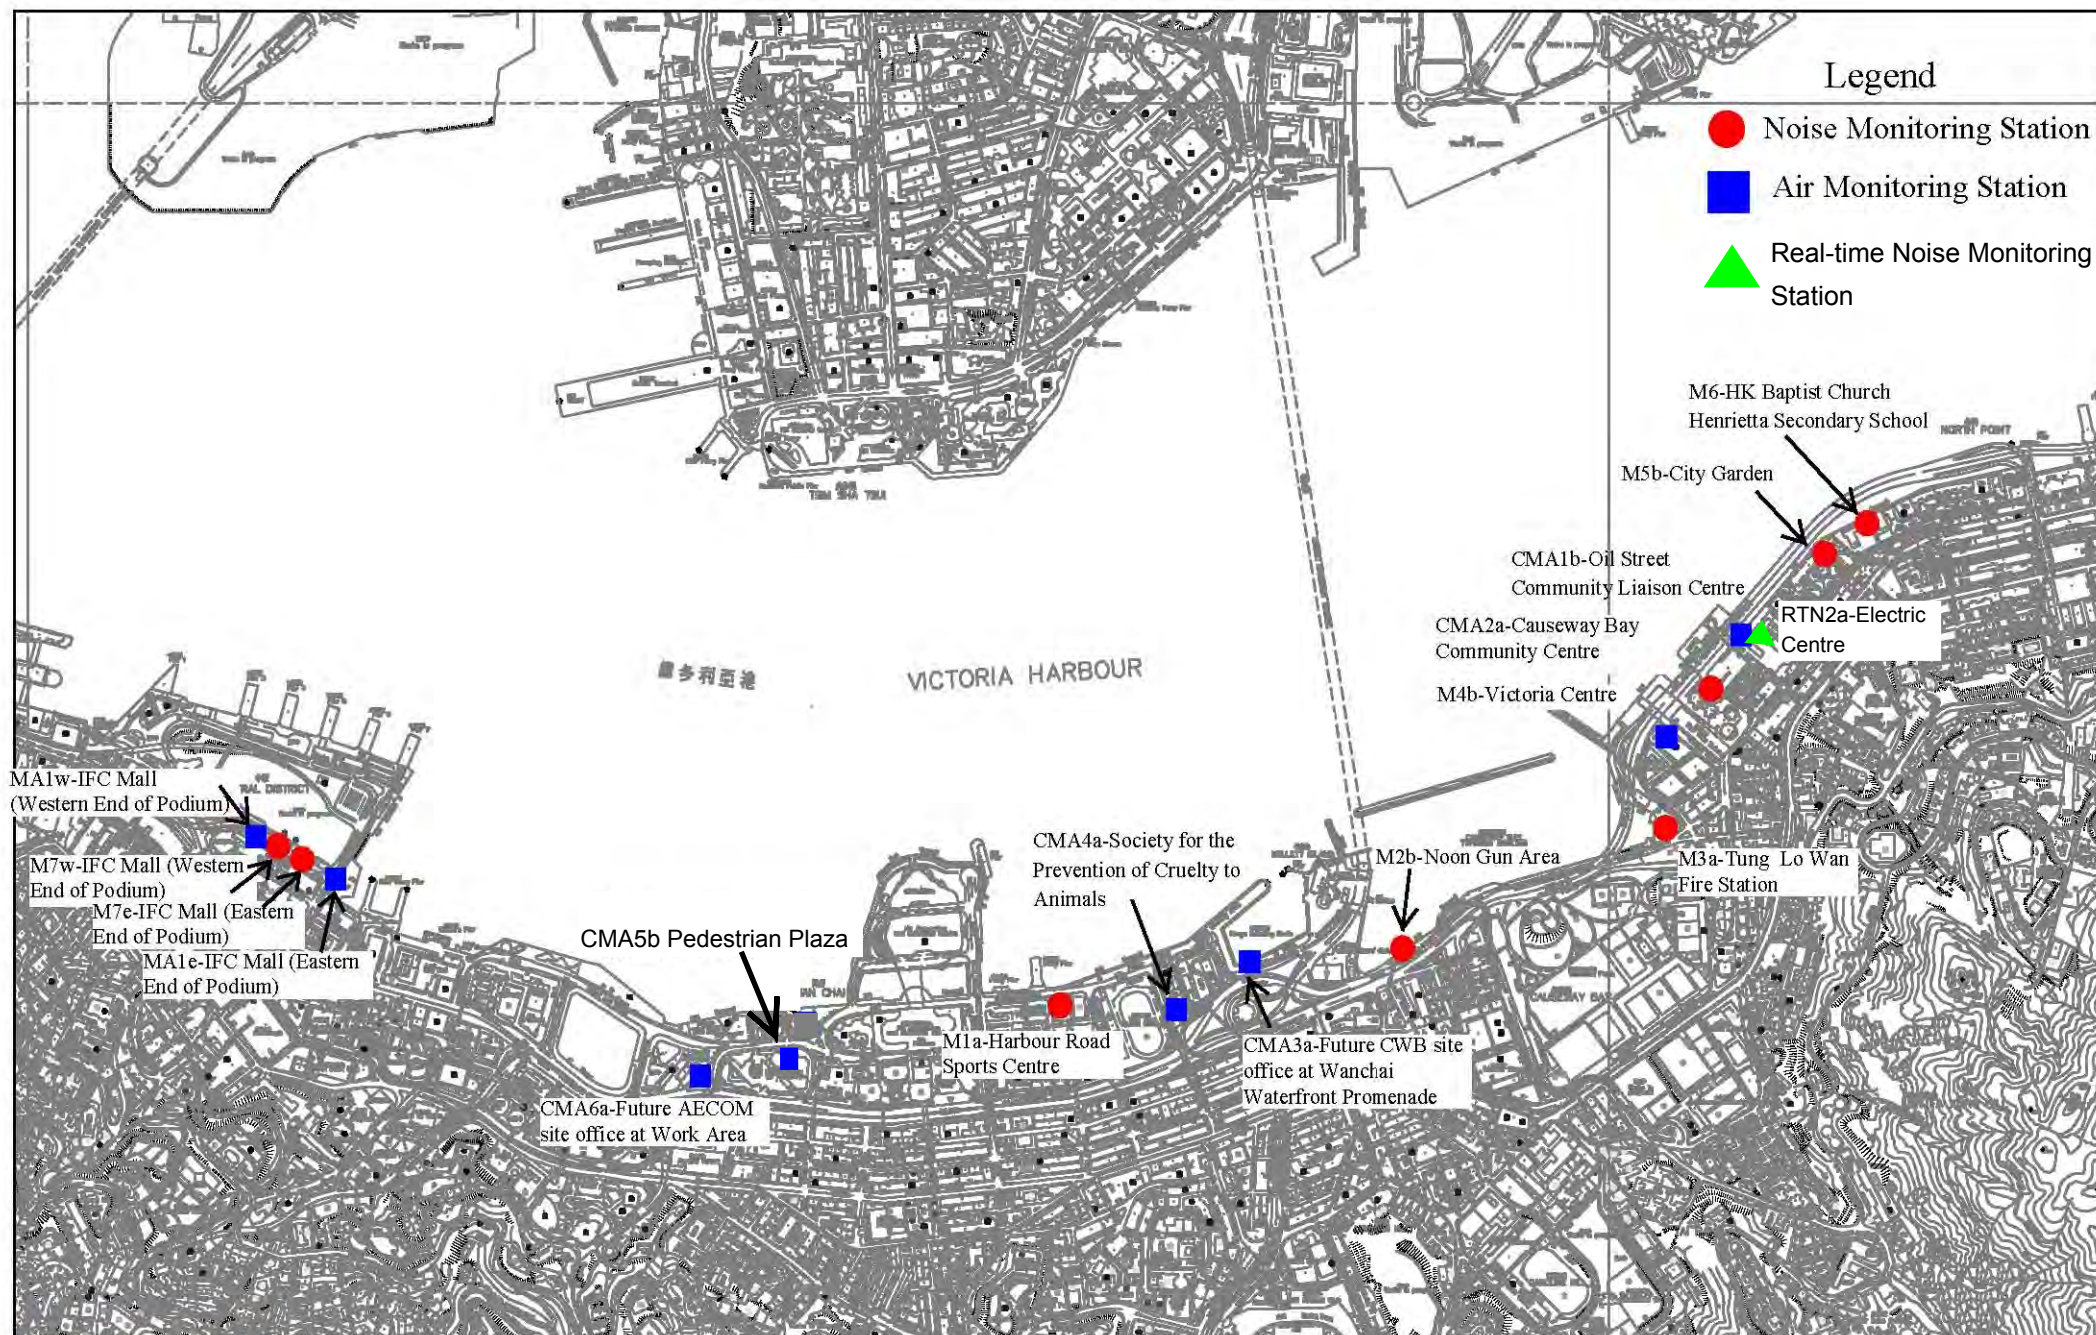

C6 AND C7: EXISTING SEAWATER INTAKE

— : ODOLIR PATROL ROUTES FOR CONSTRUCTION PHASE

● : MONITORING STATION FOR DO MEASUREMENT FOR CONSTRUCTION PHASE

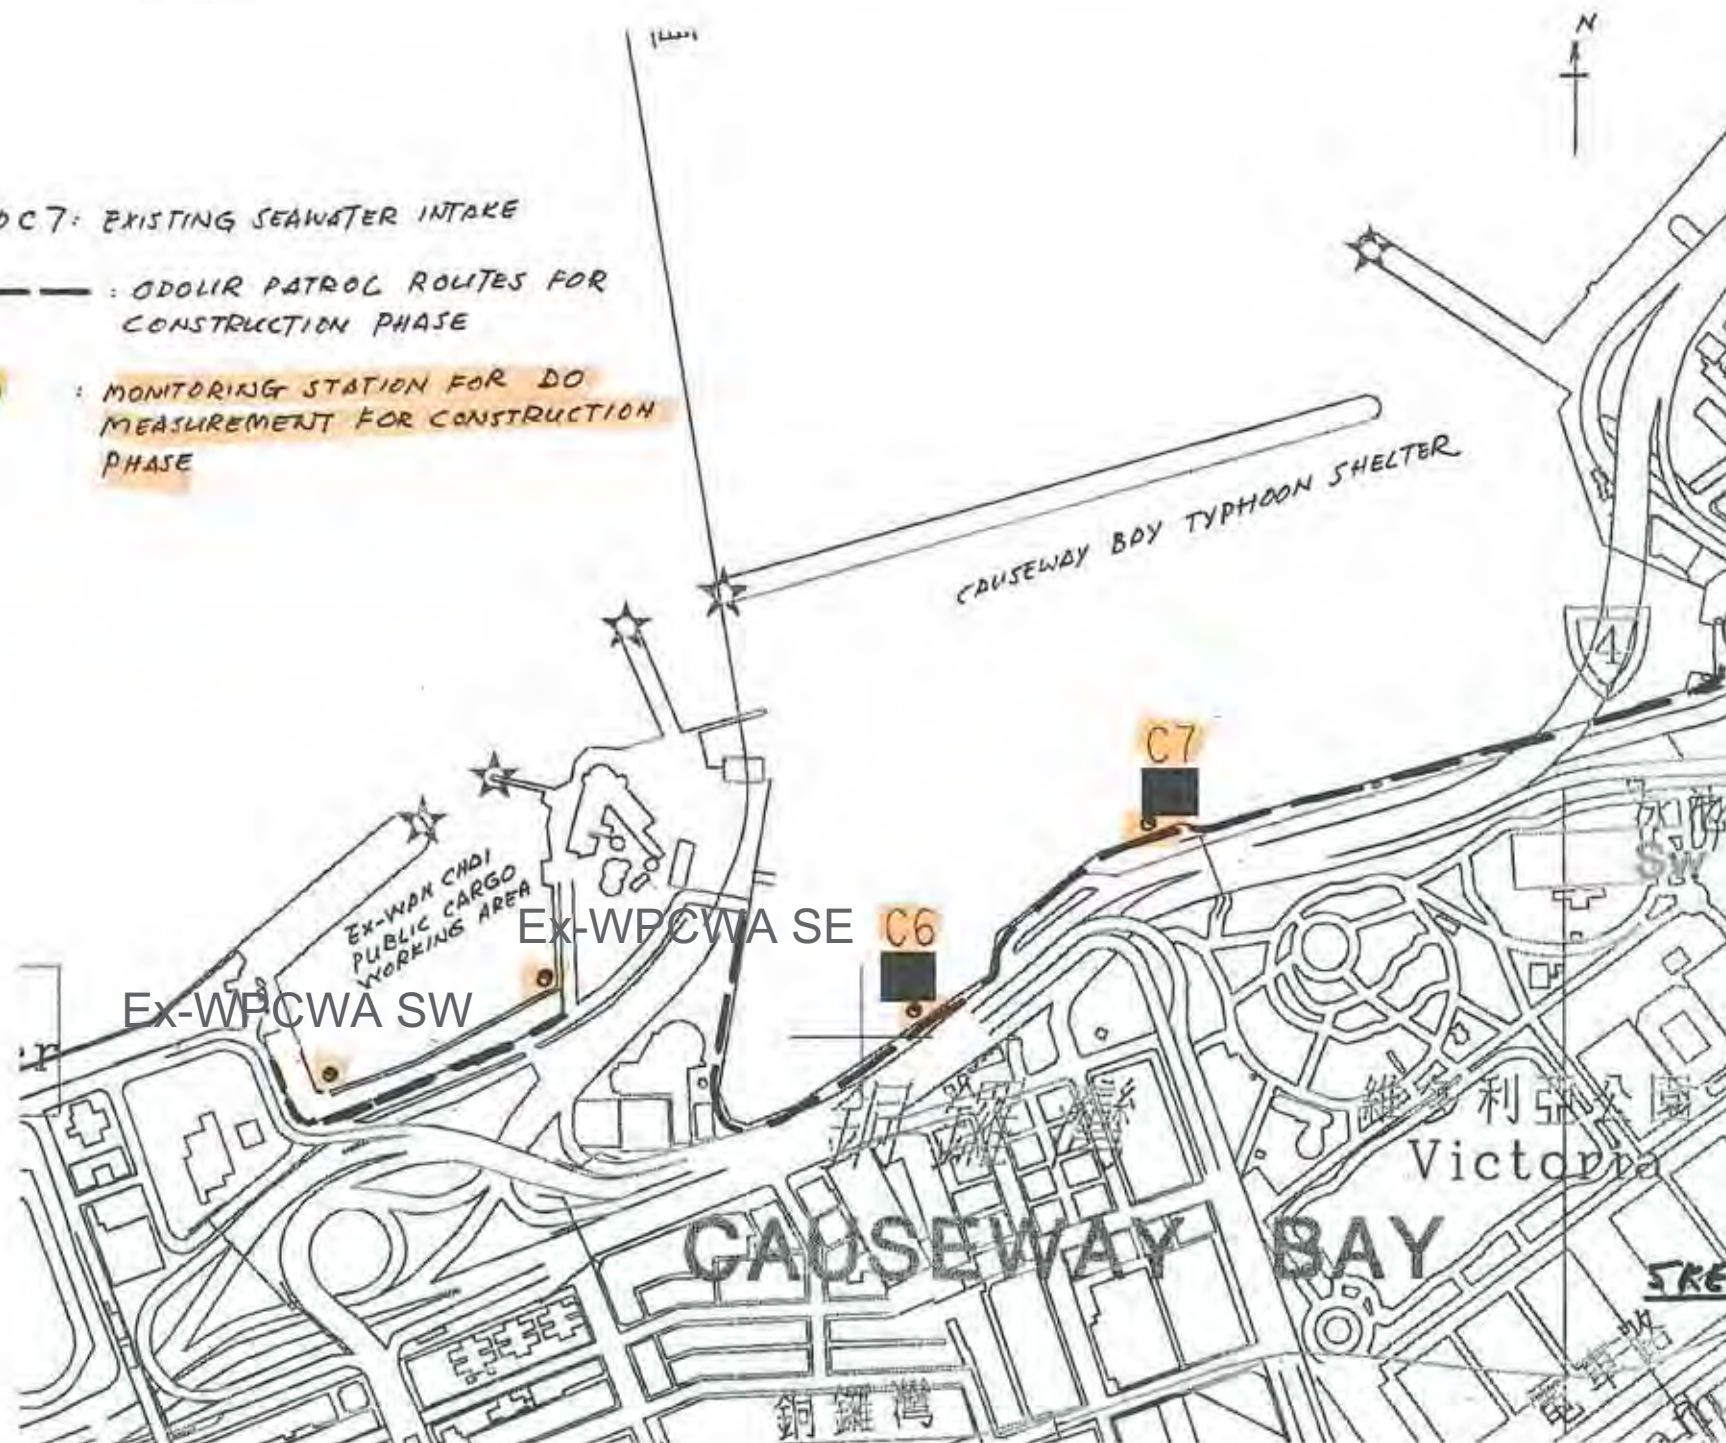



C6 AND C7: EXISTING SEAWATER INTAKE

--- : ODOR PATROL ROUTES FOR CONSTRUCTION PHASE

○ : MONITORING STATION FOR DO MEASUREMENT FOR CONSTRUCTION PHASE


● Odour Patrol Location

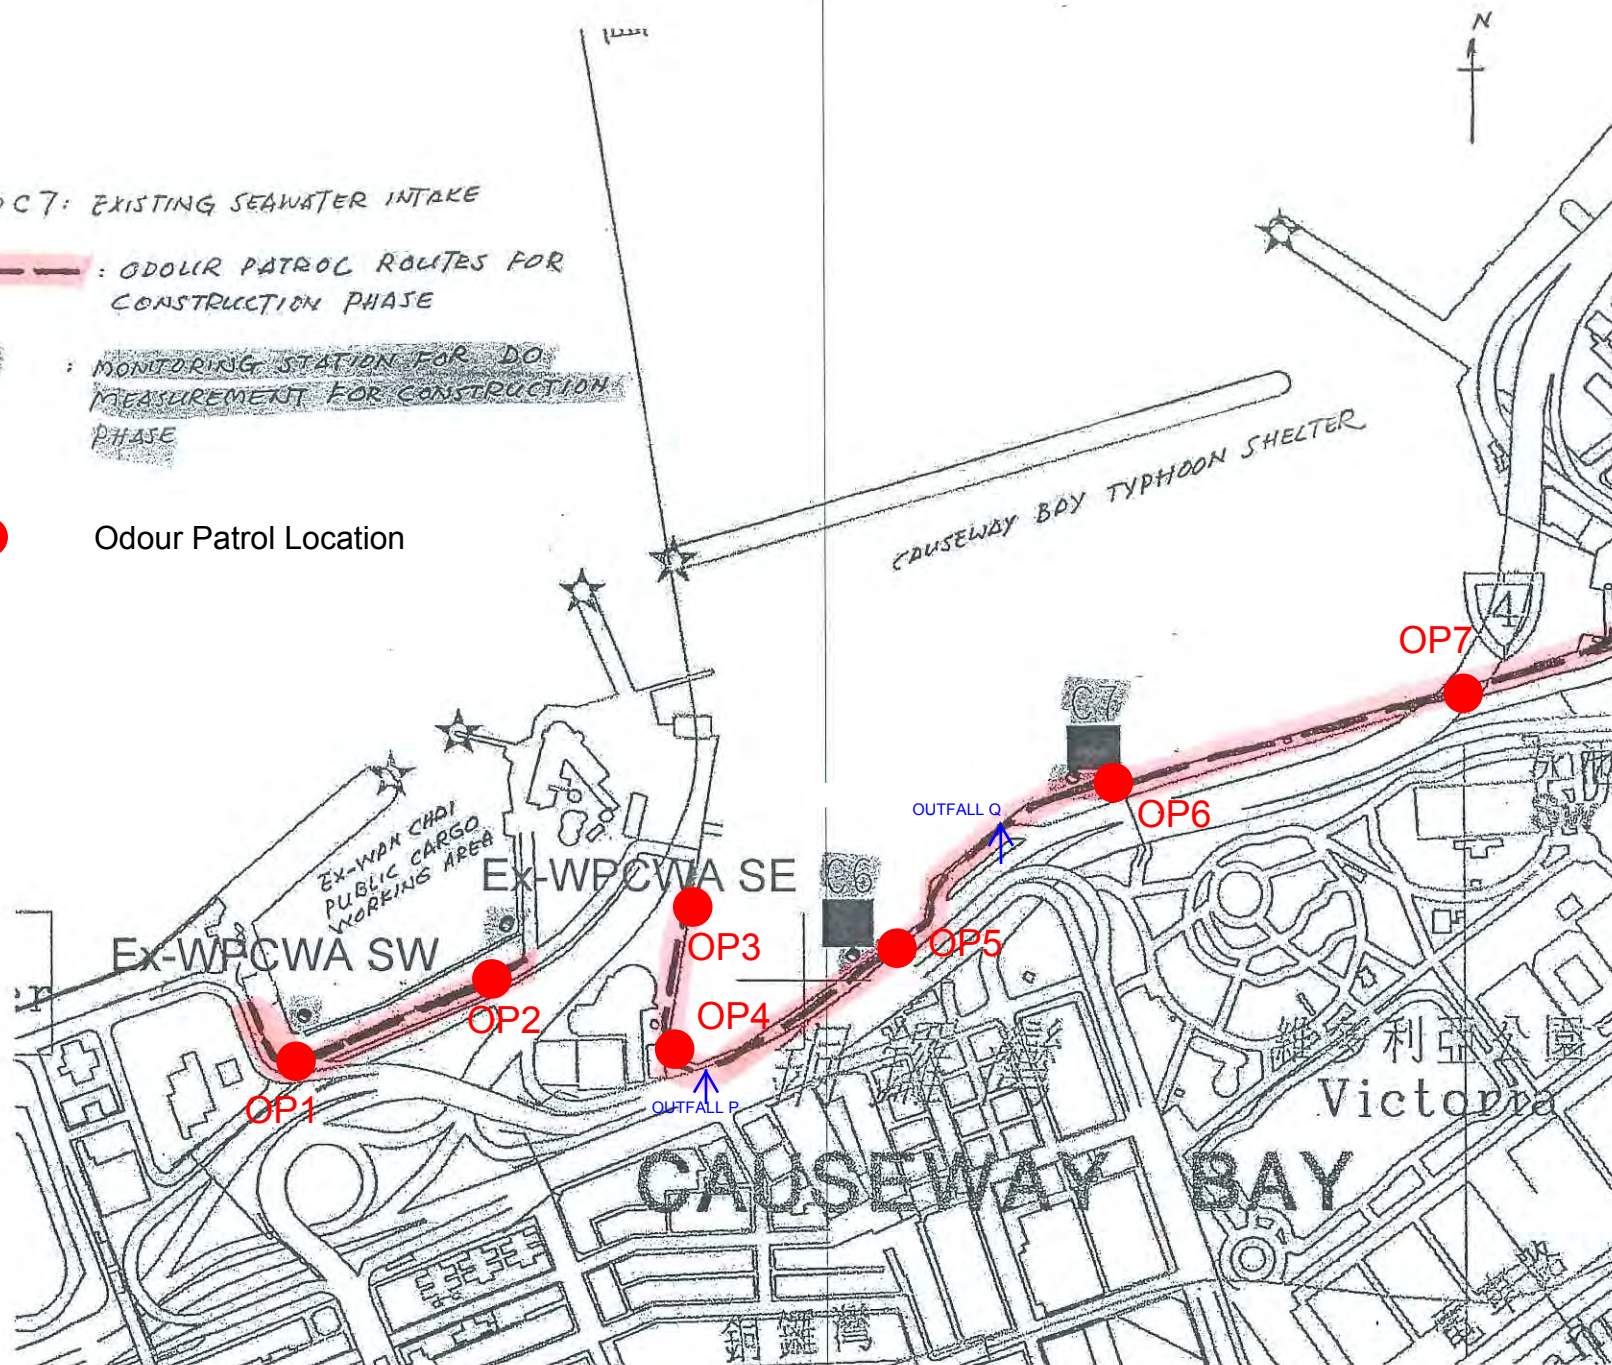

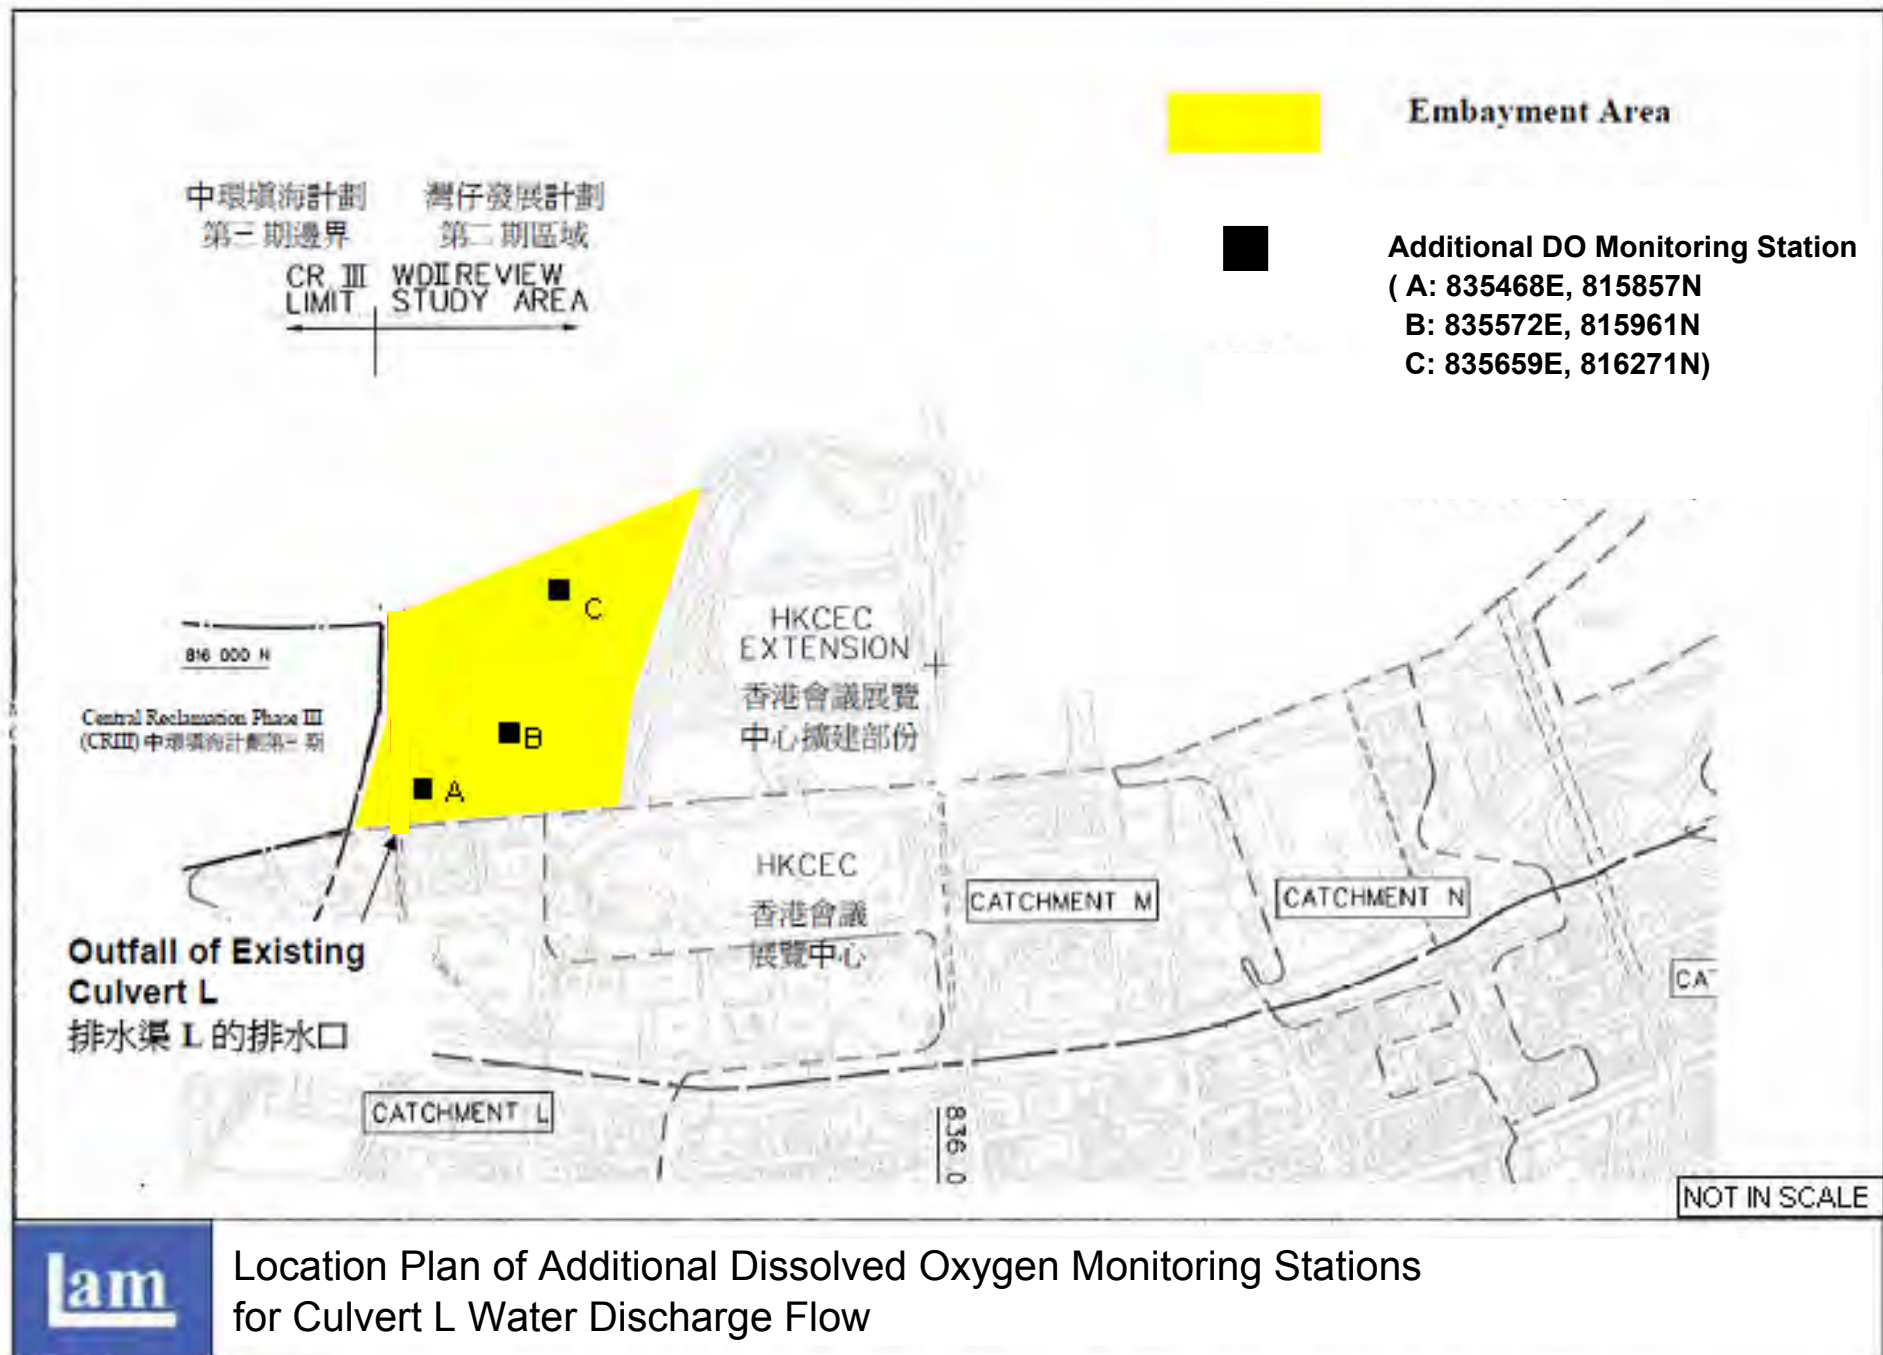

Legend


- ◆ Water Quality Monitoring Stations
- C1 Hong Kong Convention and Exhibition Centre Extension
- C2 Telecom House/ HK Academy For Performing Art/ Shui On Centre
- C3 Hong Kong Convention and Exhibition Centre Phase 1
- C4 Wan Chai Tower and Great Eagle Centre
- C5 Sun Hung Kai Centre
- C6 Proposed Exhibition Station/ World Trade Centre
- C7 Windsor House
- C8 City Garden
- C9 Provident Centre

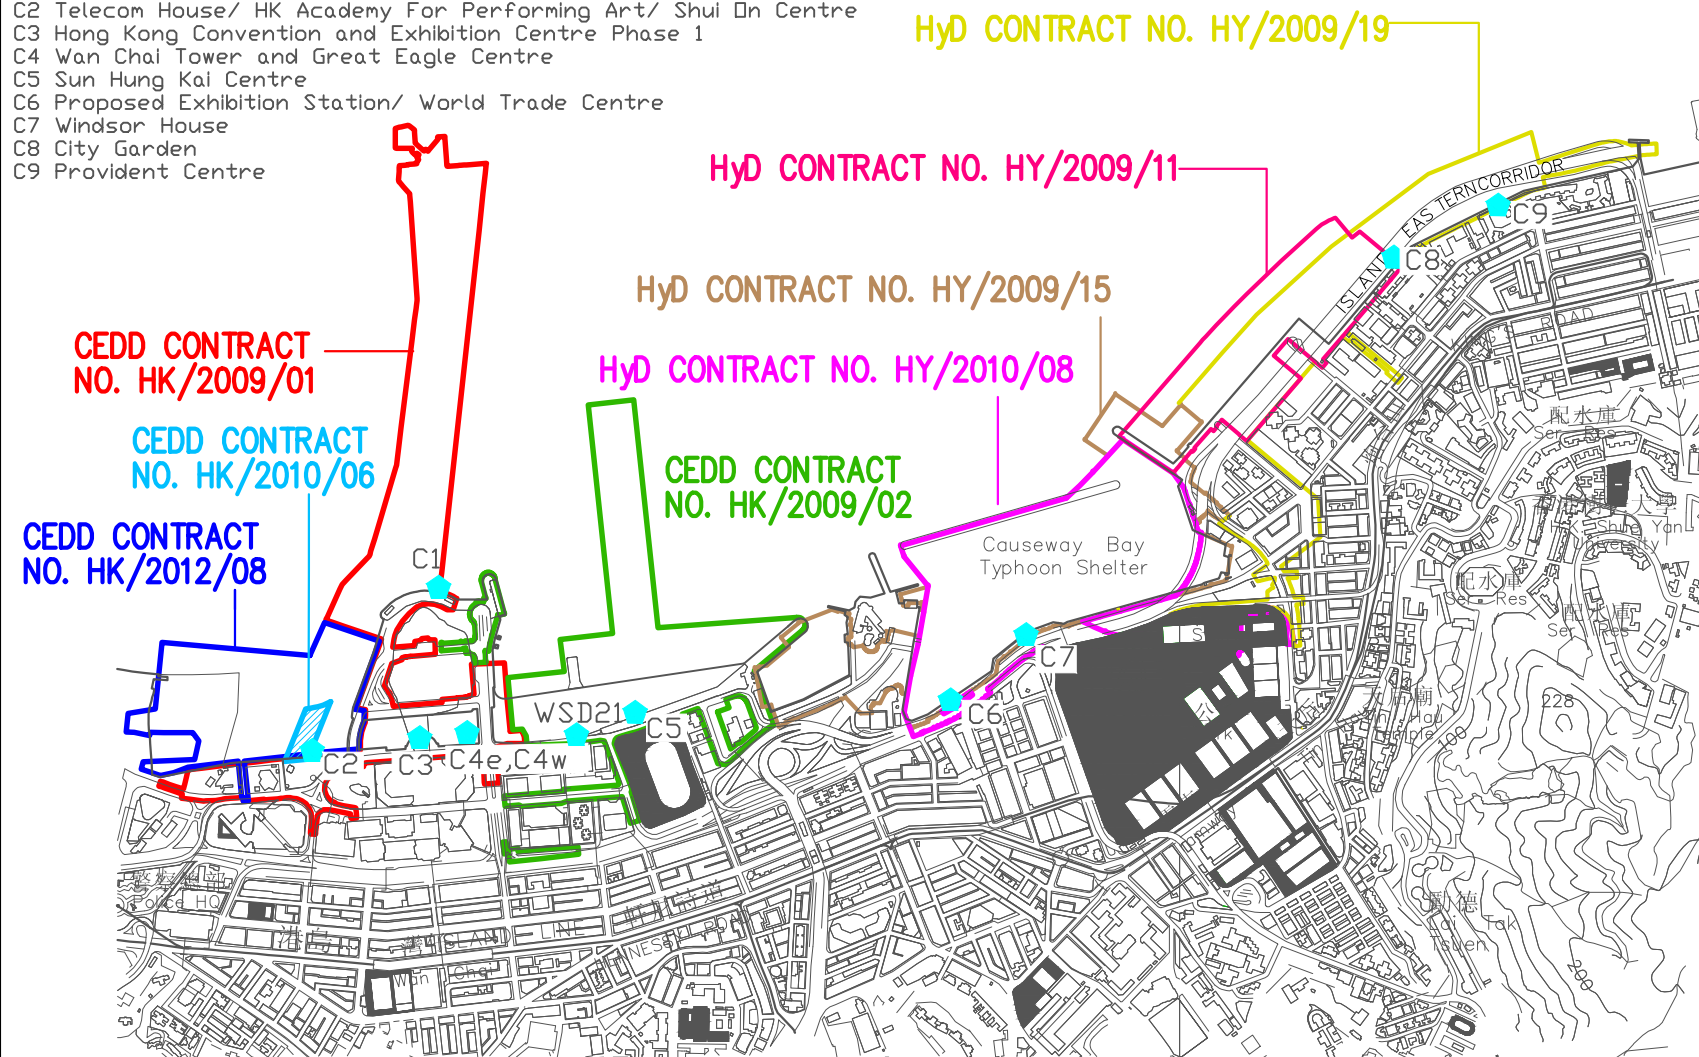

LOCATIONS OF WATER QUALITY MONITORING STATIONS

Legend

- ◆ Water Quality Monitoring Stations
- RW21-P789 (Wanchai WSD intake/ Great Eagle Centre/ China Resources Centre/ Sun Hung Kai Centre)
- C1 Hong Kong Convention and Exhibition Centre Extension
- P1 Hong Kong Convention and Exhibition Centre Phase 1
- P3 HK Academy For Performing Art
- P4 Shui On Centre
- P5 Government buildings (Wanchai Tower/ Revenue Tower/ Immigration Tower)
- C6 Proposed Exhibition Station/ World Trade Centre
- C7 Windsor House

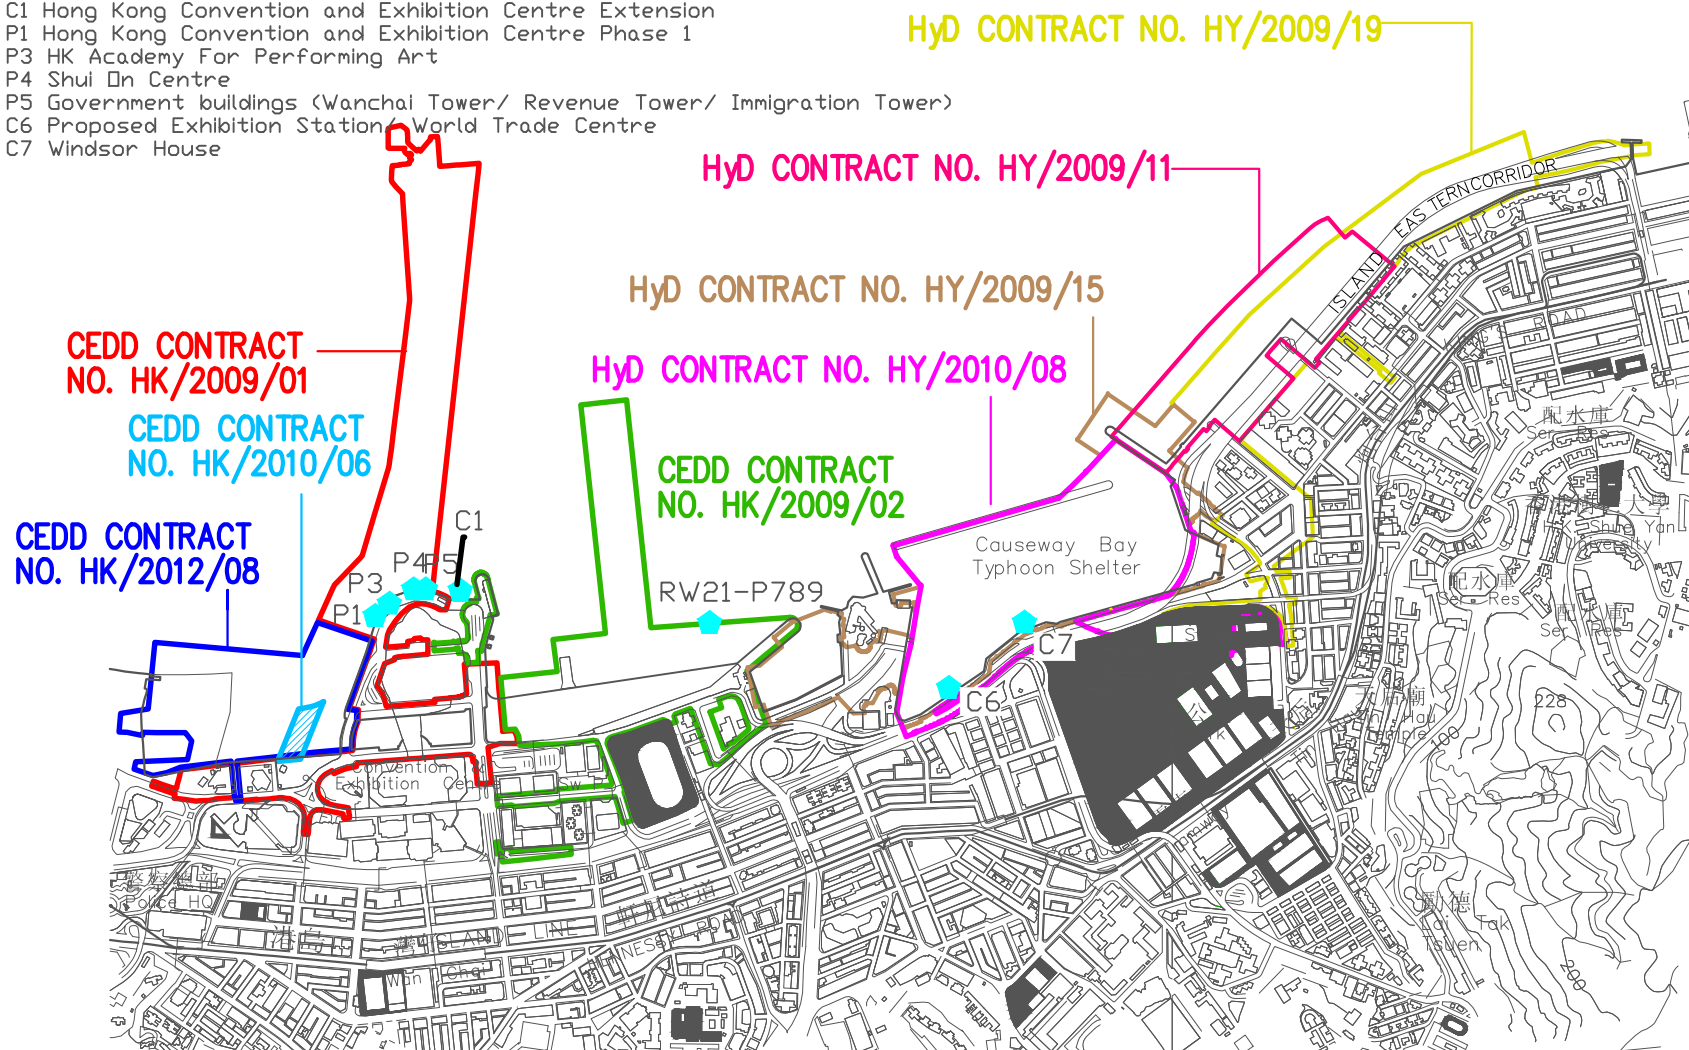

LOCATIONS OF WATER QUALITY MONITORING STATIONS

Legend

- Additional DO Monitoring Station


CEDD CONTRACT
NO. HK/2012/08

CEDD CONTRACT
NO. HK/2010/06

CEDD CONTRACT
NO. HK/2009/01

CEDD CONTRACT
NO. HK/2009/02

HyD CONTRACT
NO. HY/2009/15

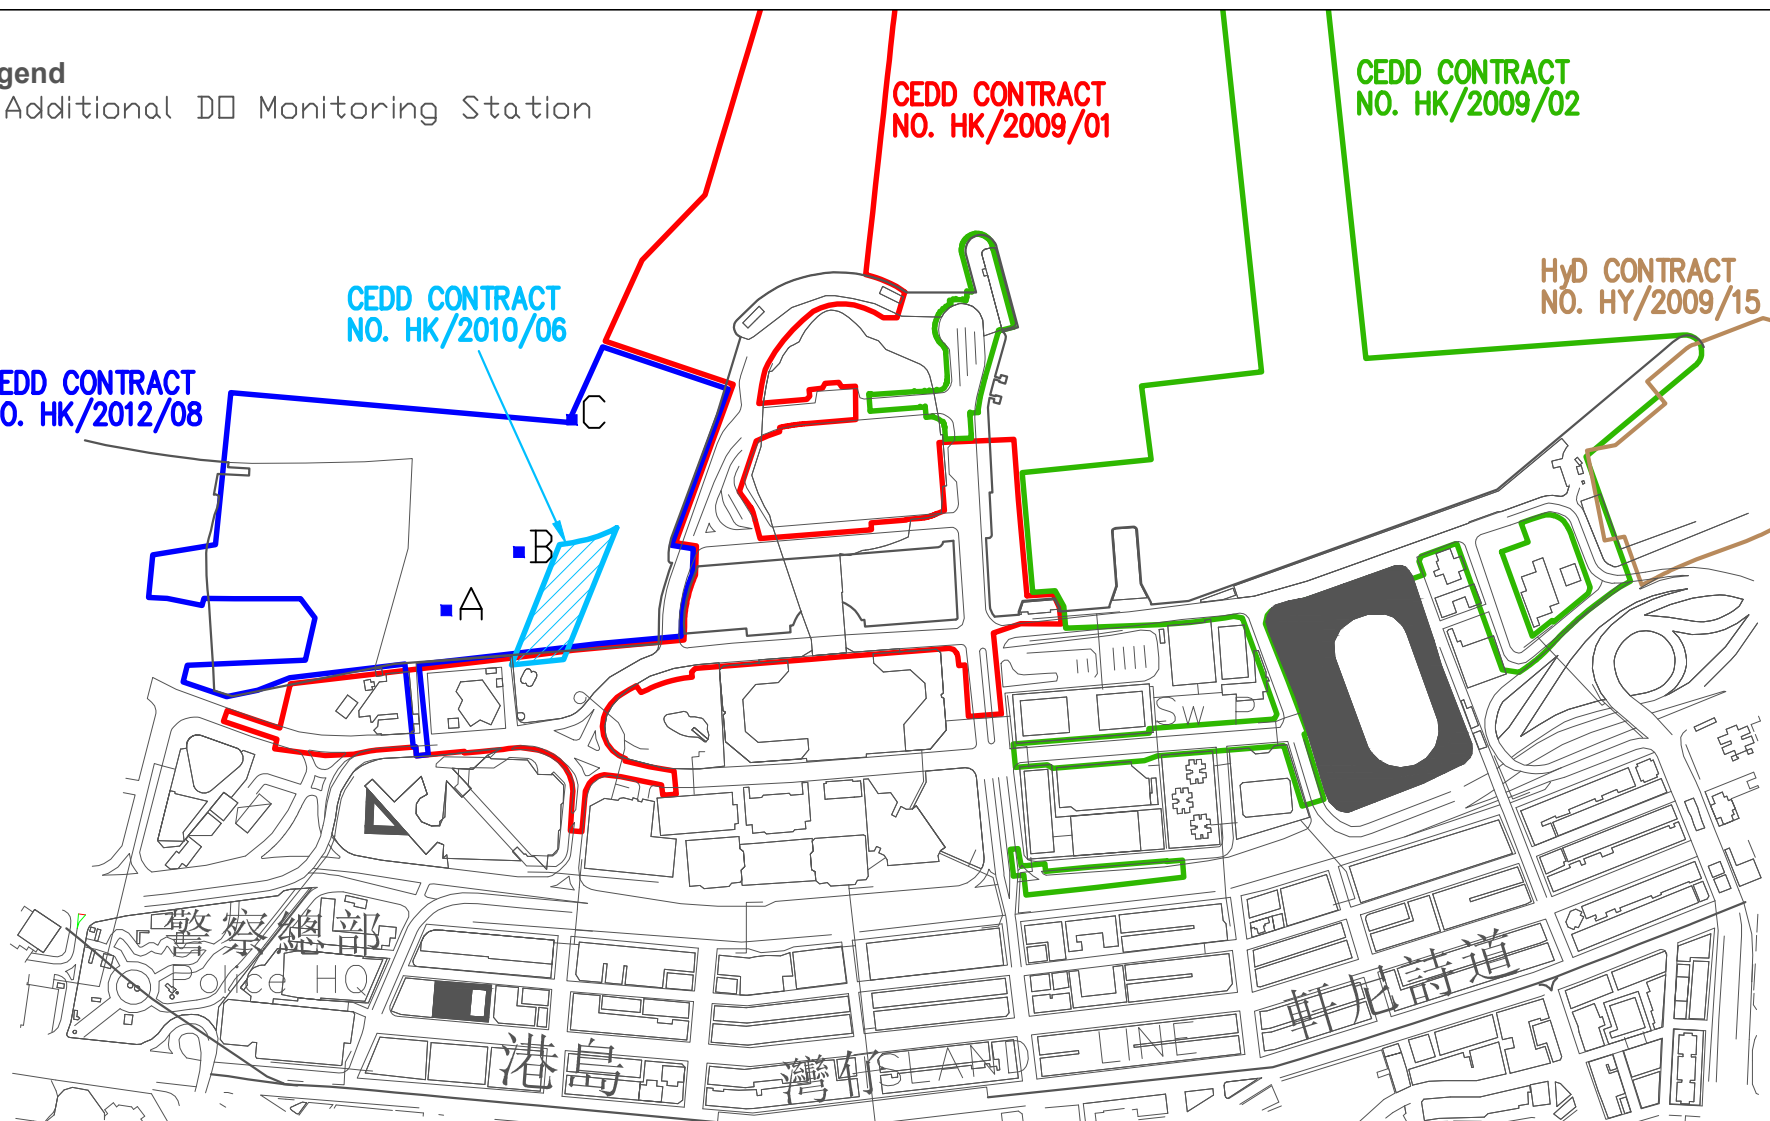

**LOCATIONS OF ADDITIONAL DISSOLVED OXYGEN MONITORING STATIONS
FOR CULVERT L WATER DISCHARGE FLOW**



Appendix 2.1

Environmental Mitigation Implementation Schedule

Environmental Mitigation Implementation Schedule

Implementation Schedule for Air Quality Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
For the Whole Project								
S3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor		√			EIAO-TM
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts. <ul style="list-style-type: none">Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition;Watering during excavation and material handling;Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; andTarpaulin covering of all dusty vehicle loads transported to, from and between site locations.	Work site / during construction	Contractor		√			

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.5.6	For the dredging activities carried out in the vicinity of Police Officers' Club, the dredging operation will be restricted to only 1 small close grab dredger to minimise the odour impact during the dredging activity. The dredging rate should be reduced as much as practicable for the area in close proximity to the Police Officers' Club. The sediments contain highly contaminated mud which may be disposed with the use of geosynthetic containers (details shall refer to Section 6), grab dredger has to be used for filling up the geosynthetic containers on barges. the dredging rate for the removal of the sediments at the south-west corner of the typhoon shelter shall be slowed down or restricted to specific non-popular hours in weekdays when it is necessary during construction.	Corner of CBTS/implementation of harbour-front enhancement	CEDD ¹		√			EIAO-TM
S3.8.8	Carry out dredging at the corner of CBTS to remove the sediment and clean the slime attached on the CBTS shoreline seawall	Corner of CBTS & CBTS shoreline seawall/implementation of harbour-front enhancement	CEDD ²		√			EIAO-TM
Operation Phase								
<i>For the Whole Project</i>								

¹ CEDD will identify an implementation agent.

² CEDD will identify an implementation agent.

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.10.2	Monthly (from July to September) monitoring of odour impacts, for a period of 5 years, is proposed during the operational phase of the Project to ascertain the effectiveness of the Enhancement Package over time, and to monitor any on-going odour impacts at the ASRs.	Planned ASRs (CBTS Breakwater)/First 5-year period of operation phase	CEDD ¹			√		EIAO-TM
For DPI – CWB (Within the Project Boundary)								
S3.6.53 – S3.6.54	The design parameters of the East and Central Ventilation Buildings as set in Tables 3.10 and 3.11	East and Central Ventilation Buildings / During operation of the Trunk Road	HyD			√		
S3.10.2	Air quality monitoring for the operation performance of the East Ventilation Building and associated East Vent Shaft will be conducted.	East Vent Shaft / During operation of the East Ventilation Building and associated East Vent Shaft	HyD			√		EIAO-TM

- Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

Appendix 2.1

Table A13.2 Implementation Schedule for Noise Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
For the Whole Project								

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S4.9.4	<p>Good Site Practice:</p> <ul style="list-style-type: none"> Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program. Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program. Mobile plant, if any, shall be sited as far away from NSRs as possible. Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum. Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from on-site construction activities. 	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
<i>For DP1 – CWB (Within the Project Boundary)</i>								

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S4.8.3 – S4.8.5	<p>Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks:</p> <ul style="list-style-type: none"> Slip road 8 tunnel Construction of diaphragm wall and substructures of the tunnel approach ramp Excavation Construction of slabs Backfill Demolition and construction of substructures for the IEC Demolition works of existing piers and crossheads of the marine section of the existing IEC <p>Use of PME grouping for the following tasks:</p> <ul style="list-style-type: none"> At-grade road construction Substructure for IECL connection 	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
<i>For DP2 – WDI Major Roads (Road P2)</i>								
S4.8.3 – S4.8.4	<p>Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks:</p> <ul style="list-style-type: none"> Temporary road diversion Resurfacing At-grade roadwork 	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
<i>For DP3 – Reclamation Works</i>								
S4.8.3 – S4.8.4	<p>Use of quiet powered mechanical equipment for the following task:</p> <ul style="list-style-type: none"> Filling behind seawall Seawall construction 	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
For DP5 – Wan Chai East Sewage Outfall								
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment for the following tasks: <ul style="list-style-type: none">Submarine pipelines (marine section) Use of quiet powered mechanical equipment and movable noise barrier for the following tasks: <ul style="list-style-type: none">Installation of a new pipeline (land section)	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
For DP6 – Cross-Harbour Water Mains from Wan Chai to Tsim Sha Tsui								
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment for the following tasks: <ul style="list-style-type: none">Submarine pipelines (marine section)	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Operation Phase								
For DP1 – CWB (Within the Project Boundary)								

Appendix 2.1

Appendix 2.1

[#] Only the steel frame for this section of noise semi-enclosure would be erected in advance during the construction of the westbound slip road.

Table A13.3 Implementation Schedule for Water Quality Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
For DP3 – Reclamation Works, DP5 (Wan Chai East Sewage Outfall), DP6 (Cross-Harbour Water Mains from Wan Chai to Tsim Sha Tsui), DP1 – CWB (within the Project Boundary)								
S5.8	A phased reclamation approach is planned for the WDII. Containment of fill within each of the reclamation phases by seawalls is proposed, with the seawall constructed first (above high water mark) with filling carried out behind the completed seawalls. Any gaps that may need to be provided for marine access will be shielded by silt curtains to control sediment plume dispersion away from the site. Filling for seawall construction should be carried out behind the silt curtain	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO
S5.8	Dredging shall be carried out by closed grab dredger for the following works: <ul style="list-style-type: none">Seawall construction in all the reclamation areas;Construction of the CWB TunnelConstruction of the proposed WSD water mains; andConstruction of the proposed Wan Chai East sewage outfall pipelines.	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO
S5.8, Figure 5.3	Dredging for the Wan Chai East sewage outfall pipelines shall not be carried out concurrently with the following activities: <ul style="list-style-type: none">Dredging along the proposed cross-harbour water mains;Dredging along the seawall in the Wan Chai Reclamation (WCR) zone (area between HKCEC Extension and PCWA).	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines																															
				Des	C	O	Dec																																
S5.8	The water body behind the temporary reclamations within the Causeway Bay typhoon shelter shall not be fully enclosed.	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																															
S5.8	As a mitigation measure, to avoid the accumulation of water borne pollutants within the temporary embayment between CR11 and HKCEC1, an impermeable barrier, suspended from a floating boom on the water surface and extending down to the seabed, will be erected by the contractor before the HKCEC1 commences. The barrier will channel the stormwater discharge flows from Culvert L to the outside of the embayment. The contractor will maintain this barrier until the reclamation works in HKCEC2W are carried out and the new Culvert L extension is constructed.	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																															
S5.8, Figure 5.3	<p>The total dredging rates in each of the marine works zones shall not be more than the maximum production rates stated in the table below. These are the production rates without considering the effect of silt curtain.</p> <table border="1"> <tr> <th colspan="2" rowspan="2">Reclamation Area</th> <th colspan="2">Maximum Dredging Rate</th> <th rowspan="2">Maximum Dredging Rate (m³ per week)</th> </tr> <tr> <th>m³ per day</th> <th>m³ per hour (for 16 hrs per day)</th> </tr> <tr> <td colspan="5">Dredging along seawall or breakwater</td> </tr> <tr> <td colspan="2">North Point Shoreline Zone (NPR)</td> <td>6,000</td> <td>375</td> <td>42,000</td> </tr> <tr> <td>Causeway Bay Shoreline Zone</td> <td>TBW</td> <td>1,500</td> <td>94</td> <td>10,500</td> </tr> <tr> <td></td> <td>TCBR</td> <td>6,000</td> <td>375</td> <td>42,000</td> </tr> <tr> <td colspan="2">PCWA Zone</td> <td>5,000</td> <td>313</td> <td>35,000</td> </tr> </table>	Reclamation Area		Maximum Dredging Rate		Maximum Dredging Rate (m³ per week)	m³ per day	m³ per hour (for 16 hrs per day)	Dredging along seawall or breakwater					North Point Shoreline Zone (NPR)		6,000	375	42,000	Causeway Bay Shoreline Zone	TBW	1,500	94	10,500		TCBR	6,000	375	42,000	PCWA Zone		5,000	313	35,000	Work site / During the construction period	Contractor		√		EIAO-TM, WPCO
Reclamation Area				Maximum Dredging Rate			Maximum Dredging Rate (m³ per week)																																
		m³ per day	m³ per hour (for 16 hrs per day)																																				
Dredging along seawall or breakwater																																							
North Point Shoreline Zone (NPR)		6,000	375	42,000																																			
Causeway Bay Shoreline Zone	TBW	1,500	94	10,500																																			
	TCBR	6,000	375	42,000																																			
PCWA Zone		5,000	313	35,000																																			

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures					Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines																								
								Des	C	O	Dec																									
	<table border="1"><tr><td colspan="2">Wan Chai Shoreline Zone (WCR)</td><td>6,000</td><td>375</td><td>42,000</td></tr><tr><td>HKCEC Shoreline Zone (HKCEC)</td><td>HKCEC Stage 1 & 3</td><td>1,500</td><td>94</td><td>10,500</td></tr><tr><td></td><td>HKCEC Stage 2</td><td>6,000</td><td>375</td><td>42,000</td></tr><tr><td colspan="2">Cross Harbour Water Mains</td><td>1,500</td><td>94</td><td>10,500</td></tr><tr><td colspan="2">Wan Chai East Submarine Sewage Pipeline</td><td>1,500</td><td>94</td><td>10,500</td></tr></table> <p>Note: 1,500 m³ per day shall be applied for construction of the western seawall of WCR1.</p>					Wan Chai Shoreline Zone (WCR)		6,000	375	42,000	HKCEC Shoreline Zone (HKCEC)	HKCEC Stage 1 & 3	1,500	94	10,500		HKCEC Stage 2	6,000	375	42,000	Cross Harbour Water Mains		1,500	94	10,500	Wan Chai East Submarine Sewage Pipeline		1,500	94	10,500						
Wan Chai Shoreline Zone (WCR)		6,000	375	42,000																																
HKCEC Shoreline Zone (HKCEC)	HKCEC Stage 1 & 3	1,500	94	10,500																																
	HKCEC Stage 2	6,000	375	42,000																																
Cross Harbour Water Mains		1,500	94	10,500																																
Wan Chai East Submarine Sewage Pipeline		1,500	94	10,500																																
S5.8, Figure 5.3	Dredging along the seawall at WCR1 shall be undertaken initially at 1,500m ³ per day for construction of the western seawall (which is in close proximity of the WSD intake), followed by partial seawall construction at the western seawall (above high water mark) to protect the adjacent intakes as much as possible from further dredging activities.					Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																								
S5.8, Figure 5.3	For dredging within the Causeway Bay typhoon shelter, seawall shall be partially constructed to protect the nearby seawater intakes from further dredging activities. For example, at TCBR1W, the southern and eastern seawalls shall be constructed first (above high water mark) so that the seawater intakes at the inner water would be protected from the impacts from the remaining dredging activities along the northern boundary.					Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																								
S5.8, Figure 5.3	Silt curtains shall be deployed around the closed grab dredgers during seawall dredging and seawall trench filling in the areas of HKCEC, WCR, TCBR and NP.					Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																								
S5.8, Figure 5.3	Silt screens shall be applied to seawater intakes at interim construction stages as stated below: <table border="1"><thead><tr><th>Interim Construction Stage</th><th>Location of Applications</th></tr></thead><tbody><tr><td>Scenario 2A in early 2009 with concurrent dredging activities at HKCEC, WCR, TPCWA.</td><td>WSD saltwater intakes at Sai Wan Ho, Quarry Bay, Sheung Wan, Wan Chai, Kowloon South Cooling water intakes for Hong Kong Convention and Exhibition Centre Extension, Hong Kong</td></tr></tbody></table>					Interim Construction Stage	Location of Applications	Scenario 2A in early 2009 with concurrent dredging activities at HKCEC, WCR, TPCWA.	WSD saltwater intakes at Sai Wan Ho, Quarry Bay, Sheung Wan, Wan Chai, Kowloon South Cooling water intakes for Hong Kong Convention and Exhibition Centre Extension, Hong Kong	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																				
Interim Construction Stage	Location of Applications																																			
Scenario 2A in early 2009 with concurrent dredging activities at HKCEC, WCR, TPCWA.	WSD saltwater intakes at Sai Wan Ho, Quarry Bay, Sheung Wan, Wan Chai, Kowloon South Cooling water intakes for Hong Kong Convention and Exhibition Centre Extension, Hong Kong																																			

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures		Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
					Des	C	O	Dec	
	TBW, NP and Water Mains Zone	Convention and Exhibition Centre Phase I, Telecom House / HK Academy for Performing Arts / Shun On Centre, Wan Chai Tower / Revenue Tower / Immigration Tower and Sun Hung Kai Centre							
	Scenario 2B in late 2009/2010 with concurrent dredging activities at Sewage Pipelines Zone and TCBR.	WSD saltwater intakes at Sheung Wan, Wan Chai Cooling water intakes for Queensway Government Offices, Excelsior Hotel, World Trade Centre and Windsor House.							
	Scenario 2C in 2011 with concurrent dredging activities at HKCEC and TCBR.	WSD saltwater intakes at Sheung Wan and Reprovisioned WSD Wan Chai saltwater intake. Cooling water intakes for MTR South, Excelsior Hotel & World Trade Centre and reprovisioned Windsor House.							
S5.8	Other mitigation measures include: <ul style="list-style-type: none">mechanical grabs, if used, shall be designed and maintained to avoid spillage and sealed tightly while being lifted. For dredging of any contaminated mud, closed watertight grabs must be used;all vessels shall be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;all hopper barges and dredgers shall be fitted with tight fitting seals to their bottom openings to prevent leakage of material;construction activities shall not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site or dumping grounds;loading of barges and hoppers shall be controlled to prevent splashing of dredged material into the surrounding water. Barges or hoppers shall not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation; and		Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO (TM-DSS)

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> before commencement of the reclamation works, the holder of Environmental Permit has to submit plans showing the phased construction of the reclamation, design and operation of the silt curtain. 							
S5.8	Silt screens are recommended to be deployed at the seawater intakes during the reclamation works period. Installation of silt screens at the seawater intake points may cause a potential for accumulation and trapping of pollutants, floating debris and refuse behind the silt screens and may lead to potential water quality deterioration at the seawater intake points. Major sources of pollutants and floating refuse include the runoff and storm water discharges from the nearby coastal areas. As a mitigation measure to avoid the pollutant and refuse entrapment problems and to ensure that the impact monitoring results are representative, regular maintenance of the silt screens and refuse collection shall be performed at the monitoring stations at regular intervals on a daily basis. The Contractor shall be responsible for keeping the water behind the silt screen free from floating rubbish and debris during the impact monitoring period.	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S5.8	Dredging of contaminated mud is recommended as a mitigation measures for control of operational odour impact from the Causeway Bay typhoon shelter. In recognition of the potential impacts caused by dredging activities close to the seawater intakes, only 1 small close grab dredger shall be operated within the typhoon shelter (for the dredging to mitigate odour impact) at any time to minimize the potential impact. Double silt curtains shall be deployed to fully enclose the closed grab dredger during the dredging operation. In addition, an impermeable barrier, suspended from a floating boom on the water surface and extended down to the seabed, shall be erected to isolate the adjacent intakes as much as possible from dredging activities. For example, if dredging is to be carried out at the southwest corner of the typhoon shelter, physical barriers shall be erected to west of the cooling water intake for Excelsior Hotel so that the intake would be shielded from most of the SS generated from the dredging operation to the west of the intake. For area in close proximity of the cooling water intake point, the dredging rate shall be reduced as much as practicable. Site audit and water quality monitoring shall be carried out at the seawater intakes during the dredging operations. Daily monitoring of SS at the cooling water intake shall be carried out, and 24 hour monitoring of turbidity at the intakes shall be implemented during the dredging activities. If the monitoring results indicate that the dredging operation has caused significant changes in water quality conditions at the seawater intakes, appropriate actions shall be taken to stop the dredging and mitigation measures such as slowing down the dredging rate shall be implemented.	Causeway Bay typhoon shelter/Implementation of harbour-front enhancement.	CEDD ³		√			WPCO

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
For the Whole Project								
S5.8	<ul style="list-style-type: none">Construction Runoff and Drainageuse of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;a sediment tank constructed from pre-formed individual cells of approximately 6 - 8 m3 capacity can be used for settling ground water prior to disposal;oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall have a bypass to prevent flushing during periods of heavy rain;precautions and actions to be taken when a rainstorm is imminent or forecast, and during or after rainstorms. Particular attention shall be paid to the control of any silty surface runoff during storm events;on-site drainage system shall be installed prior to the commencement of other construction activities. Sediment traps shall be installed in order to minimise the sediment loading of the effluent prior to discharge;All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge shall be adequately designed for the controlled release of storm flows. All sediment control measures shall be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage shall be reinstated to its original condition when the construction work is finished or the temporary diversion is no longer	<ul style="list-style-type: none">Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO (TM-DSS)

³ CEDD will identify an implementation agent.

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p>required.</p> <ul style="list-style-type: none"> All fuel tanks and store areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity. 							
	<ul style="list-style-type: none"> Minimum distances of 100 m shall be maintained between the storm water discharges and the existing or planned WSD flushing water intakes during construction phase. 							
S5.8	<p><i>Sewage from Construction Work Force</i></p> <p>Construction work force sewage discharges on site shall be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage shall be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices.</p>	Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO (TM-DSS)
S5.8	<p><i>Floating Debris and Refuse</i></p> <p>Collection and removal of floating refuse shall be performed at regular intervals on a daily basis. The contractor shall be responsible for keeping the water within the site boundary and the neighbouring water free from rubbish.</p>	Work site and adjacent water / During the construction period.	Contractor		√			WPCO

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S5.8	<p><i>Storm Water Discharges</i></p> <p>Minimum distances of 100 m shall be maintained between the existing or planned stormwater discharges and the existing or planned WSD flushing water intakes.</p>	Work site and adjacent water / During the design and construction period.	Contractor	√	√			WPCO
Operation Phase								
DPI – CWB (within the Project Boundary)								
S5.8	<p>For the operation of CWB, a surface water drainage system would be provided to collect road runoff. The following operation stage mitigation measures are recommended to ensure road runoff would comply with the TM under the WPCO:</p> <ul style="list-style-type: none"> The drainage from tunnel sections shall be directed through petrol interceptors to remove oil and grease before being discharged to the nearby foul water manholes. Petrol interceptors shall be regularly cleaned and maintained in good working condition. Oily contents of the petrol interceptors shall be properly handled and disposed of, in compliance with the requirements of the Waste Disposal Ordinance. Sewage arising from ancillary facilities of CWB (for examples, car park, 	CWB/During design and operational period	HyD/TD ³	√		√		WPCO

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p>control room, ventilation and administration buildings and tunnel portals) shall be connected to public sewerage system. Sufficient capacity in public sewerage shall be made available to the proposed facilities.</p> <ul style="list-style-type: none"> Road drainage shall also be provided with adequately designed silt trap to minimize discharge of silty runoff. The design of the operational stage mitigation measures for CWB shall take into account the guidelines published in ProPECC PN 5/93 "Drainage Plans subject to Comment by the EPD." All operational discharges from the CWB into drainage or sewerage systems are required to be licensed by EPD under the WPCO. 							

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

³ if employ Management, Operation and Maintenance (MOM) Contract

Appendix 2.1

Table A13.4 Implementation Schedule for Waste Management

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
For DP3 – Reclamation Works								
S6.7.2	<p><i>Marine Sediments</i></p> <p>The dredged marine sediments would be loaded onto barges, transported to and disposed of at the designated disposal sites at South of Cheung Chau, East of Ninepin, East of Tung Lung Chau, South of Tsing Yi or East of Sha Chau to be allocated by the MFC depending on their level of contamination or at other disposal sites after consultation with the MFC and EPD. In accordance with the ETWB TCW No. 34/2002, the contaminated material must be dredged and transported with great care. The mitigation measures recommended in Section 5 of the EIA Report shall be incorporated. The dredged contaminated sediment must be effectively isolated from the environment upon final disposal and shall be disposed of at the Type 2 confined marine disposal contaminated mud pit.</p>	Work site / During the construction period	Contractor		√			ETWB TCW No. 34/2002
S6.7.3	Based on the biological screening results, the Category H (>10xLCEL) sediment which failed the biological testing would require Type 3 special disposal. The volume of Category H sediment from the Causeway Bay typhoon shelter which would require special disposal arrangements is estimated to be approximately 0.05 Mm ³ . A feasible containment method is proposed whereby the dredged sediments are sealed in geosynthetic containers and, at the disposal site, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping, thereby meeting the requirements for fully confined mud disposal.							

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.5	It will be the responsibility of the Contractor to satisfy the appropriate authorities that the contamination levels of the marine sediment to be dredged have been analysed and recorded. According to the ETWB TCW No. 34/2002, this will involve the submission of a formal Sediment Quality Report to the DEP, at least 3 months prior to the dredging contract being tendered							
S6.7.6	<p>During transportation and disposal of the dredged marine sediments requiring Type 1 and Type 2 disposal, the following measures shall be taken to minimise potential impacts on water quality:</p> <ul style="list-style-type: none"> Bottom opening of barges shall be fitted with tight fitting seals to prevent leakage of material. Excess material shall be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved. 							

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> Monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP. Barges or hopper barges shall not be filled to a level that would cause the overflow of materials or sediment laden water during loading or transportation. 							
S6.6.12	<p>Floating Refuse</p> <p>During the construction phase, the project proponent's contractor will be responsible for the collection of any refuse within their works area. Floating booms will be provided on the water surface to confine the refuse from the working barges as well as to avoid the accumulation of pollutants within temporary embayment as mentioned in Table 13.3.</p>	Work site / During the construction period	Contractor		√			
For the Whole Project								

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.7	<p>Good Site Practices</p> <p>Recommendations for good site practices during the construction activities include:</p> <ul style="list-style-type: none"> nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; training of site personnel in proper waste management and chemical waste handling procedures; provision of sufficient waste disposal points and regular collection for disposal; appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and a recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites). 	Work site / During the construction period	Contractor		√			Waste Disposal Ordinance (Cap.354)

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.8	<p><i>Waste Reduction Measures</i></p> <p>Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; to encourage collection of aluminium cans, PET bottles and paper, separate labelled bins shall be provided to segregate these wastes from other general refuse generated by the work force; any unused chemicals or those with remaining functional capacity shall be recycled; use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&D material. prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill; proper storage and site practices to minimise the potential for damage or contamination of construction materials; and plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 	Work site / During planning and design stage, and construction stage	Contractor	√	√			

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.10	<p><i>General Refuse</i></p> <p>General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material.</p> <p>A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.</p>	Work site / During the construction period	Contractor		√			Public Health and Municipal Services Ordinance (Cap. 132)
S6.7.11	<p><i>Chemical Wastes</i></p> <p>After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.</p>	Work site / During the construction period	Contractor		√			Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.7.12	<p><i>Construction and Demolition Material</i></p> <p>C&D material shall be sorted on-site into inert C&D material (that is, public fill) and C&D waste. All the suitable inert C&D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.</p>	Work site / During the construction period	Contractor		√			ETWB TCW No. 33/2002, 31/2004, 19/2005

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.13	In order to monitor the disposal of public fill and C&D waste at public filling facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.	Work site / During the construction period	Contractor and Independent Environmental Checker		√			ETWB TCW No. 31/2004
S6.7.14	<p><i>Bentonite Slurry</i></p> <p>The disposal of residual used bentonite slurry shall follow the good practice guidelines stated in ProPECC PN 1/94 "Construction Site Drainage" and listed as follows:</p> <ul style="list-style-type: none"> If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis. If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters. If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal. 	Work site / During the construction period	Contractor		√			ProPECC PN 1/94

* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Appendix 2.1

Table A13.5 Implementation Schedule for Land Contamination

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
For the Whole Project								
S.12.6	<ul style="list-style-type: none">The contaminated site shall be cleaned up before commencement of site clearance and construction work at the concerned area which may disturb the ground.	A King Marine / Before commencement of construction activities at A King Marine.	Project proponent for the re-provisioned Tin Hau Temple	√				<p>“Guidance Notes for Investigation and Remediation of Contaminated Sites of Petrol Filling Stations, Boatyards, and Car Repair/Dismantling Workshops” published by EPD, HKSAR</p> <p>EPD ProPECC Note No. 3/94</p>
S7.10	<p>During soil remediation works, the Contractor for the excavation works shall take note of the following points for excavation:</p> <ul style="list-style-type: none">Excavation profiles must be properly designed and executed;In case the soil to be excavated is situated beneath the groundwater table, it may be necessary to lower the groundwater table by installing well points or similar means;Quantities of soil to be excavated must be estimated;It maybe necessary to split quantities of soil according to soil type, degree and nature of contamination.Temporary storage of soil at intermediate depot or on-site	A King Marine / During soil remediation works	Contractor	√				<p>Air Pollution Control Ordinance</p> <p>Noise Control Ordinance</p> <p>Waste Disposal Ordinance</p> <p>Waste Disposal (Chemical Waste) (General) Regulation</p>

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	maybe required. The storage site shall include protection facilities for leaching into the ground. eg. Liner maybe required.							
	<ul style="list-style-type: none"> Supply of suitable clean backfill materials is needed after excavation. Care must be taken of existing buildings and utilities. Precautions must be taken to control of ground settlement Speed controls for vehicles shall be imposed on dusty site areas. Vehicle wheel and body washing facilities at the site's exit points shall be established and used. <p>The following environmental mitigation measures shall be strictly followed during the operation and/or maintenance of the CS/S facilities:</p>							Water Pollution Control Ordinance

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p><u>Air Quality Mitigation Measures</u></p> <ul style="list-style-type: none"> The loading, unloading, handling, transfer or storage of cement shall be carried out in an enclosed system. The loading, unloading, handling, transfer or storage of other materials which may generate airborne dust emissions such as untreated soil and oversize materials sorted out from the screening plant and stabilized soil stockpiled in the designated handling area, shall be carried out in such a manner to prevent or minimise dust emissions. These materials shall be adequately wetted prior to and during the loading, unloading and handling operations. All practicable measures, including speed controls for vehicles, shall be taken to prevent or minimize the dust emission caused by vehicle movement. Tarpaulin or low permeable sheet shall be put on dusty vehicle loads transported between site locations. 							
	<p><u>Noise Mitigation Measures</u></p> <ul style="list-style-type: none"> The mixing facilities shall be sited as far as practicable to the nearby noise sensitive receivers. Simultaneous operation of mixing facilities and other equipment shall be avoided. Mixing process and other associated material handling activities shall be properly scheduled to minimise potential cumulative noise impact on the nearby noise sensitive receivers. Construction Noise Permit shall be applied for the operation of powered mechanical equipment during restricted hours (if any). 							

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p><u>Water Quality Mitigation Measures</u></p> <ul style="list-style-type: none"> Stockpile of untreated soil shall be covered as far as practicable to prevent the contaminated material from leaching out. The leachate shall be discharged following the requirements of WPCO. <p><u>Waste Mitigation Measures</u></p> <ul style="list-style-type: none"> Treated oversize materials will be used as filling material for backfilling within the site. Sorted materials of size smaller than 5 cm will be collected and transferred to the mixing plant for further decontamination treatment. Stabilized soils shall be broken into suitable size for backfilling or reuse on site. A high standard of housekeeping shall be maintained within the mixing plant area. If necessary, there shall be clear and separated areas for stockpiling of untreated and treated materials. 							

* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Appendix 2.1

Table A13.6 Implementation Schedule for Marine Ecology

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Construction Phase								
For the Whole Project - Schedule 3 DP								
S.9.7.2	Alternative design of the Trunk Road constructed in tunnel shall be adopted to avoid permanent reclamation in CBTS and ex-PWCA Basin.	-	CEDD/HyD	√				EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
For DP3 – Reclamation Works								
S.9.7.3	Translocation of those potentially affected coral colonies to the nearby suitable habitats such as Junk Bay is recommended. A detailed translocation plan (including translocation methodology, monitoring of transplanted corals, etc.) should be drafted and approval by AFCD during the detailed design stage of the Project.	Ex-PCWA Basin and along seawall next to a public pier which is about 250 m away from the CBTS	CEDD/HyD	√				EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S.9.7.4	During dredging and filling operations, a number of mitigation measures to control water quality shall be adopted to confine sediment plume within reclamation area and protect marine fauna in proximity to the reclamation. The mitigation measures include the following: <ul style="list-style-type: none"> • Installation of silt curtains during dredging activities • Use of tightly-closed grab dredger • Reduction of dredging rate • Control of grab descending speed • Construction of leading edges of seawall in the early stages of the reclamation works 	Work site / during construction phase	Contractor		√			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
	• Adoption of multiple-phase construction schedule							

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S.9.7.6	To minimize potential disturbance impacts on the foraging ardeid population in the CBTS, particularly in the area near the A King Shipyard, appropriate mitigation measures shall be adopted particularly during the construction phase. The following measures are recommended: <ul style="list-style-type: none"> • Use of Quiet Mechanical Plant during the construction phase shall be adopted wherever possible. • Adoption of multiple-phase construction schedule. • General measures to reduce noise generated during the construction phase (see noise impact assessment) shall be effectively implemented. 	Work site / during construction phase	Contractor		√			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
S.9.7.7	Seawalls shall be constructed in advance around the reclamation areas within the area of the CBTS to screen adjacent feeding ground from construction phase activities, reduce noise disturbance to the associated seabirds and also to restrict access to this habitat adjacent to works areas by ship traffic.	Work site / during construction phase	Contractor		√			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
S.9.7.8	Loss of artificial seawall habitats shall be reinstated by the construction of about 1 km vertical wave absorbing seawall along the coastlines of the new reclamation around the HKCEC and at North Point. The new seawalls are expected to provide large area of hard substrata for settlement and recruitment of intertidal fauna similar to those previously recorded from existing intertidal habitats.	Work site / during construction phase	Contractor		√			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.

*Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Appendix 2.1

Table A13.7 Implementation Schedule for Landscape and Visual

EIA Ref	Environmental Protection Measures / Mitigation Measures		Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
					Des	C	O	Dec	
Construction Phase									
For the Whole Project									
Table 10.5	CM1	Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM2	Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM3	Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM4	Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM5	Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6	Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
For DP1 – CWB (Within the Project Boundary)									
Table 10.5	CM1	Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM2	Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM3	Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM4	Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM5	Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
For DP2 – WDII Major Roads (Road P2)								
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
For DP3 – Reclamation Works								
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
For DP5 – Wan Chai East Sewage Outfall								
Refer to EIA-058/2001 Table 10.13	CM2 Minimisation of works areas.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM3 Erection of decorative hoardings.	Work site / During Construction Phase	Contractor		√			EIAO TM

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Refer to EIA-058/2001 Table 10.13	CM4 Control night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM5 Minimisation of disruption to public by effective programming of the works.	Work site / During Construction Phase	Contractor		√			EIAO TM
For DP6 – Cross-Harbour Water Mains from Wan Chai to Tsim Sha Tsui								
Refer to EIA-058/2001 Table 10.13	CM2 Minimisation of works areas.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM3 Erection of decorative hoardings.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM4 Control night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM5 Minimisation of disruption to public by effective programming of the works.	Work site / During Construction Phase	Contractor		√			EIAO TM
Operation Phase								
For the Whole Project - Schedule 3 DP								
Table 10.6, Figure 10.5.1-10.5.5	OM1 Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	CEDD/HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM2 Shrub and Climbing Plants to soften proposed structures.	Work site / During Design Stage and Operation Phases	CEDD/HyD	√	√	√		ETWB TCW 2/2004

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 10.6, Figure 10.5.1-10.5.5	OM3 Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	CEDD/HyD/	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM4 Aesthetic design of proposed waterfront promenade.	Work site / During Design Stage and Operation Phases	CEDD ⁴	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM5 Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	CEDD/HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM6 Aesthetic design of roadside amenity areas.	Work site / During Design Stage and Operation Phases	CEDD/HyD	√	√	√		ETWB TCW 2/2004
For DP1 – CWB (Within the Project Boundary)								
Table 10.6, Figure 10.5.1-10.5.5	OM1 Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM2 Shrub and Climbing Plants to soften proposed structures	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM3 Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM5 Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM6 Aesthetic design of roadside amenity areas.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
For DP2 – WDII Major Roads (Road P2)								

⁴ CEDD will identify an implementation agent

Appendix 2.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 10.6, Figure 10.5.1-10.5.5	OM1 Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	CEDD/HyD		√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM3 Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	CEDD/HyD		√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM5 Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	CEDD/HyD		√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM6 Aesthetic design of roadside amenity areas	Work site / During Design Stage and Operation Phases	CEDD/HyD		√	√		ETWB TCW 2/2004
For DP3 – Reclamation Works								
Table 10.6, Figure 10.5.1-10.5.5	OM4 Aesthetic design of proposed waterfront promenade.	Work site / During Design Stage and Operation Phases	CEDD ⁵	√	√	√		ETWB TCW 2/2004

*Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

⁵ CEDD will identify an implementation agent



Appendix 3.1

Action and Limit Level

Action and Limit Level

Action and Limit Level for Noise Monitoring

Time Period	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A) ^{Note 1}

Note 1:

- 70dB(A) and 65 dB(A) for schools during normal teaching periods and school examination periods, respectively.
- If works are to be carried out during the restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

Action and Limit Level for Air Monitoring

Monitoring Location	1-hour TSP Level in $\mu\text{g}/\text{m}^3$		24-hour TSP Level in $\mu\text{g}/\text{m}^3$	
	Action Level	Limit Level	Action Level	Limit Level
CMA1b ^{Note 2}	320.1	500	176.7	260
CMA2a	323.4	500	169.5	260
CMA3a ^{Note 2}	311.3	500	171.0	260
CMA4a	312.5	500	171.2	260
CMA5b ^{Note 2}	332.0	500	181.0	260
CMA6a ^{Note 2}	300.1	500	187.3	260

Note 2:

- As per facing owner's rejection in allowing the implementation of long-term air quality impact monitoring at their premises, alternative monitoring stations and justification were proposed for IEC verification and EPD approval.
- The established Action and Limit Levels from the baseline air monitoring will be adopted to the alternative monitoring stations.

Action and Limit Level for Water Monitoring

Parameters	Dry Season		Wet Season	
	Action	Limit	Action	Limit
WSD Salt Water Intake				
SS in mg L^{-1}	13.00	14.43	16.26	19.74
Turbidity in NTU	8.04	9.49	10.01	11.54
DO in mg/L	3.66	3.28	3.17	2.63
Cooling Water Intake				
SS in mg L^{-1}	15.00	22.13	18.42	27.54
Turbidity in NTU	9.10	10.25	11.35	12.71
DO in mg/L	3.36	2.73	3.02	2.44

Remarks:

- Action and Limit Level for the wet season are applied after the EPD approval of Updated EM&A Manual on 29 April 2011.

Action and Limit Levels for Odour Patrol

Parameters	Action	Limit
Odour Nuisance (from odour intensity analysis or odour patrol)	<ul style="list-style-type: none"> When two documented complaint are received; or Odour Intensity of 2 is measured from odour intensity analysis. 	<ul style="list-style-type: none"> Five or more consecutive genuine documented complaints within a week; or Odour Intensity of 3 or above is measured from odour intensity analysis.






Appendix 4.1

Noise Monitoring Graphical Presentations




Graphic Presentation of Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

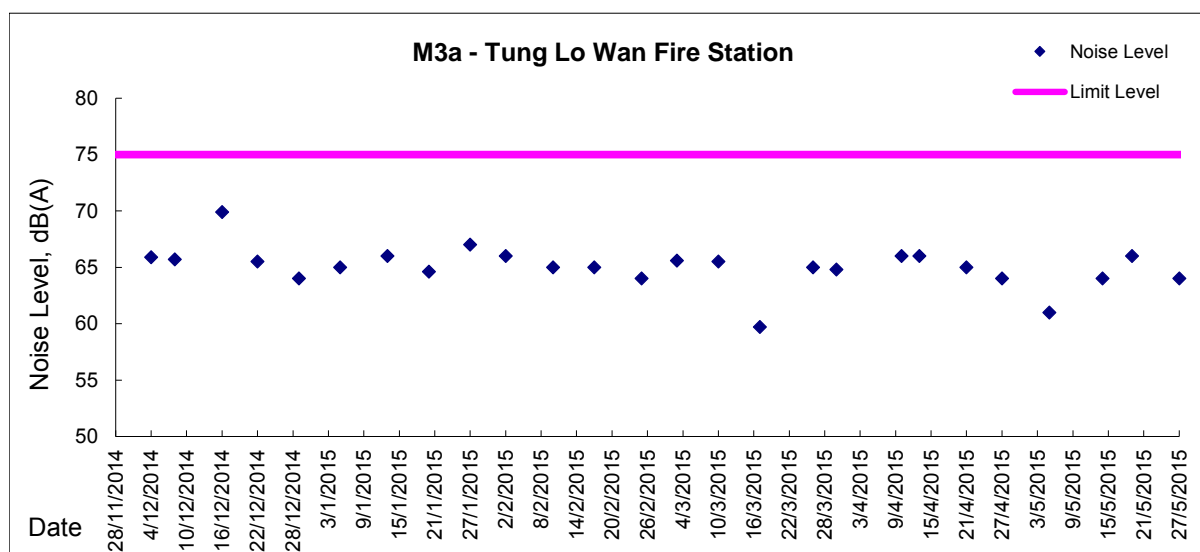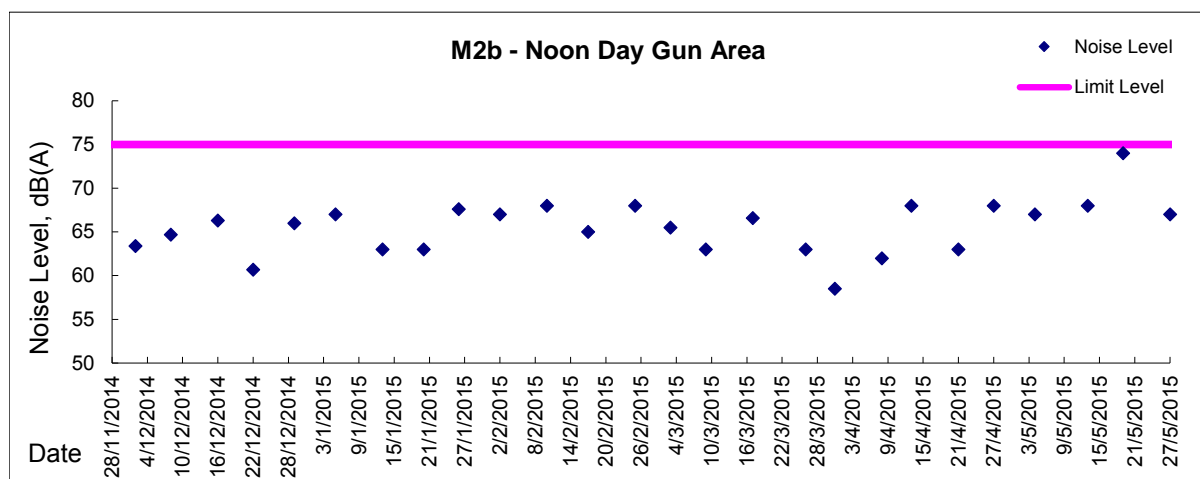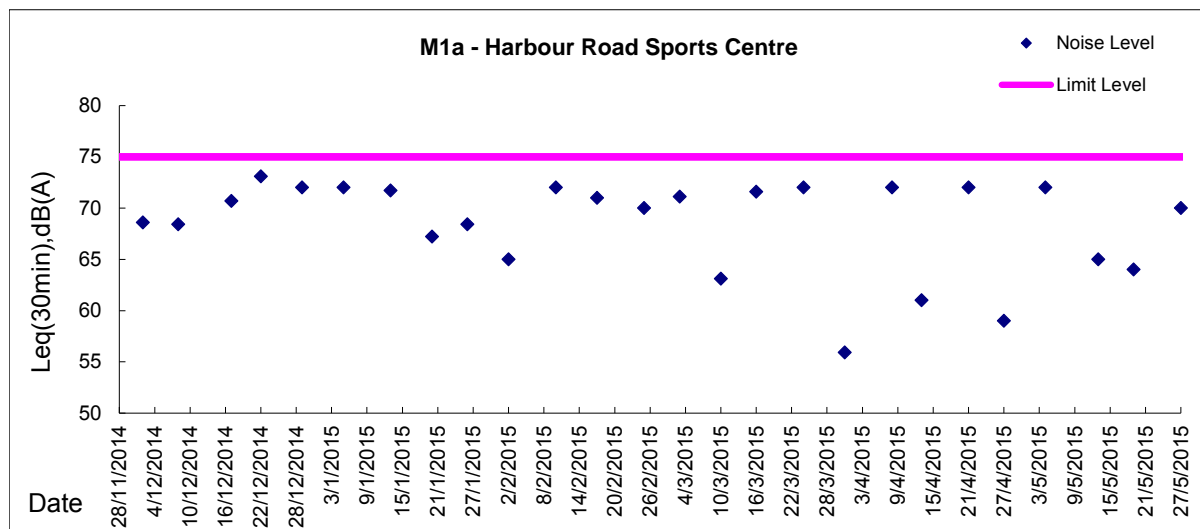

Graphic Presentation of Noise Monitoring Result


Day Time (0700 - 1900hrs on normal weekdays)

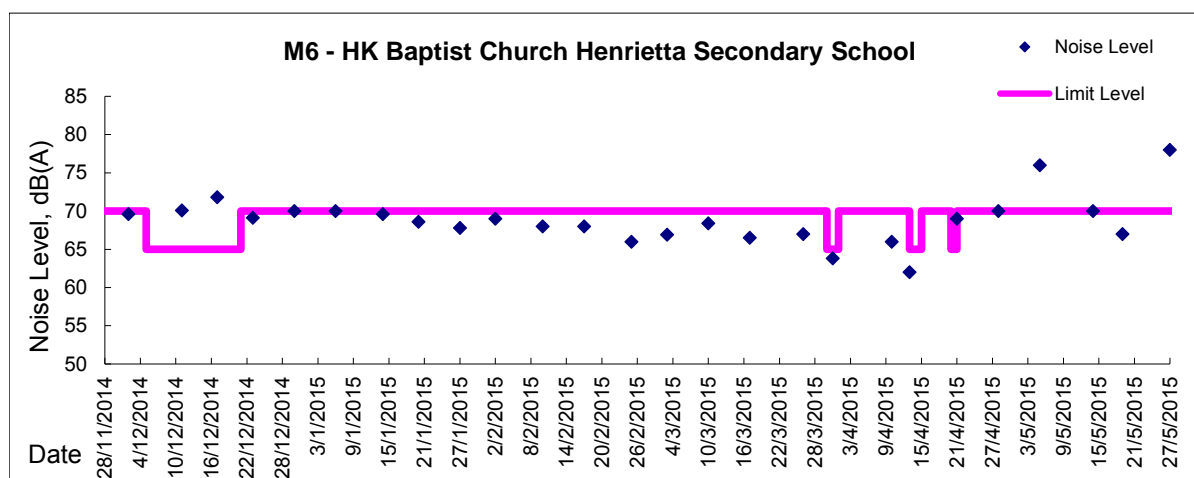
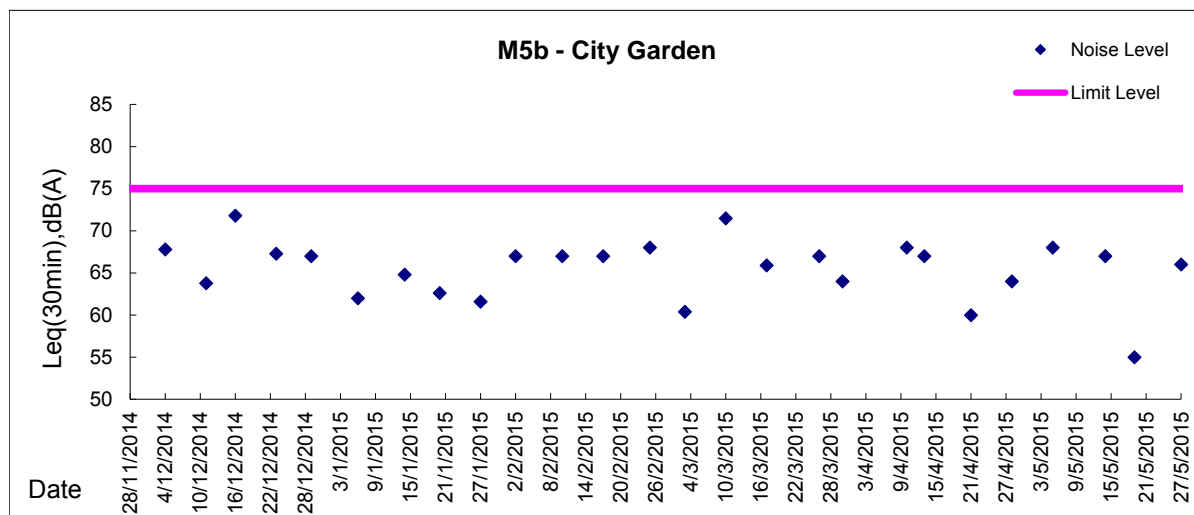
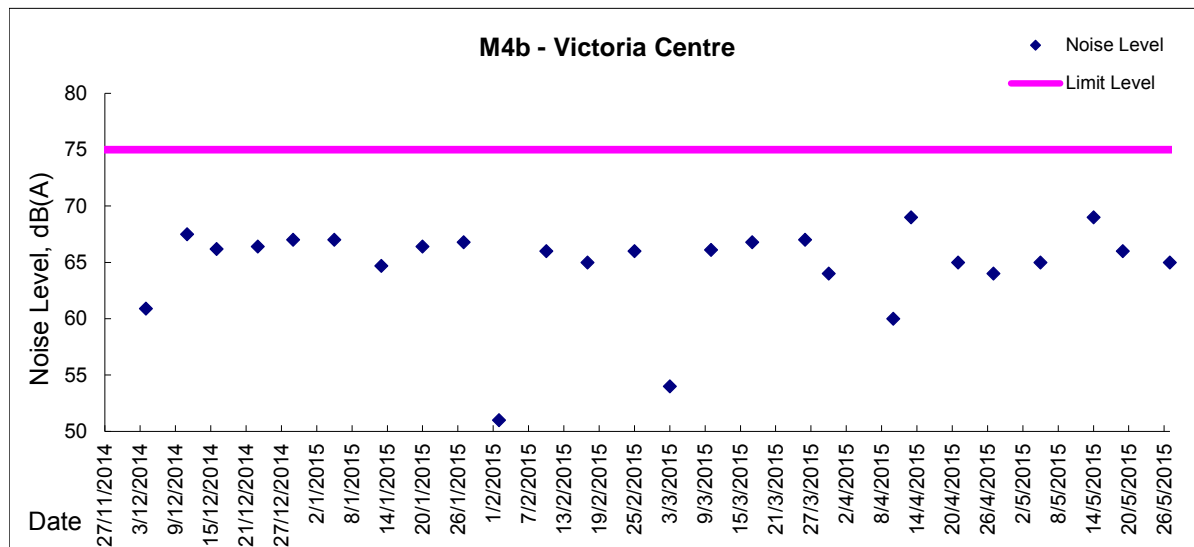







Appendix 4.2
Air Quality Monitoring Graphical Presentations

Graphic Presentation of 1 hour TSP Result



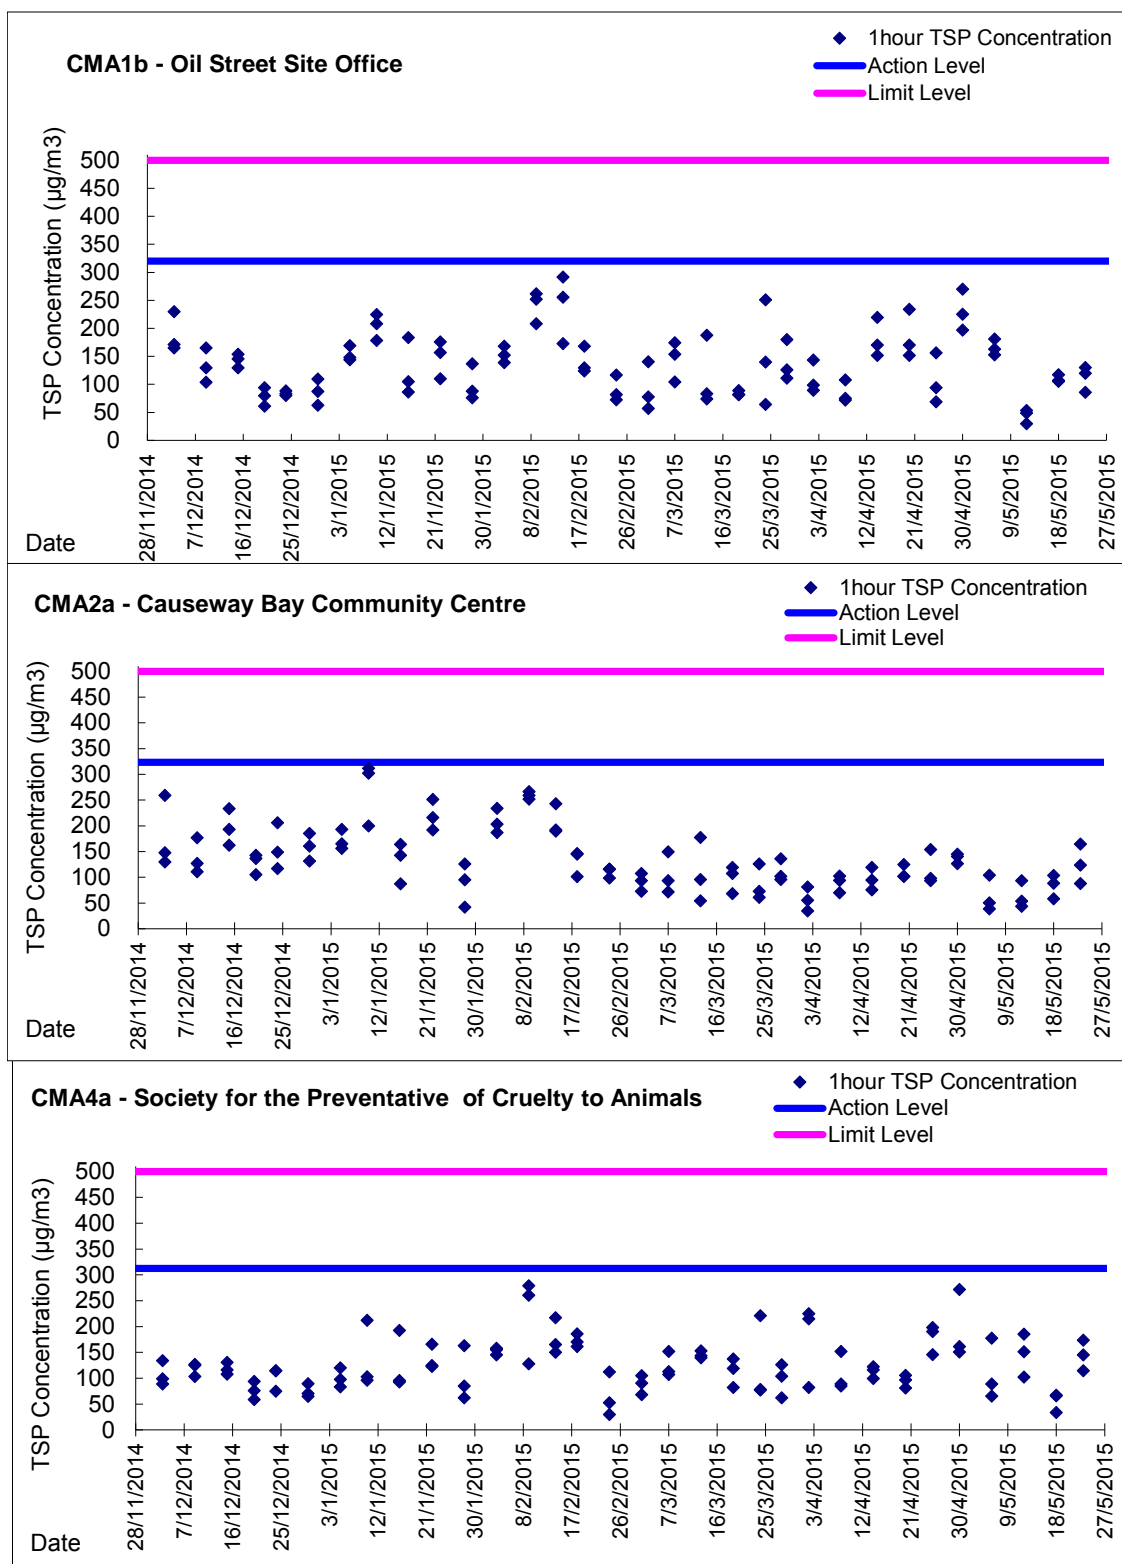


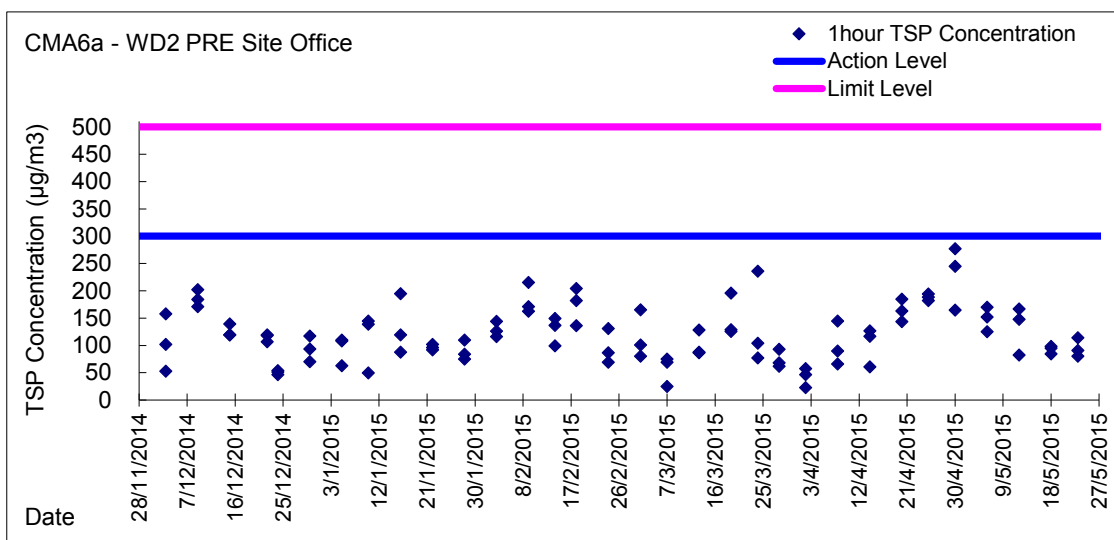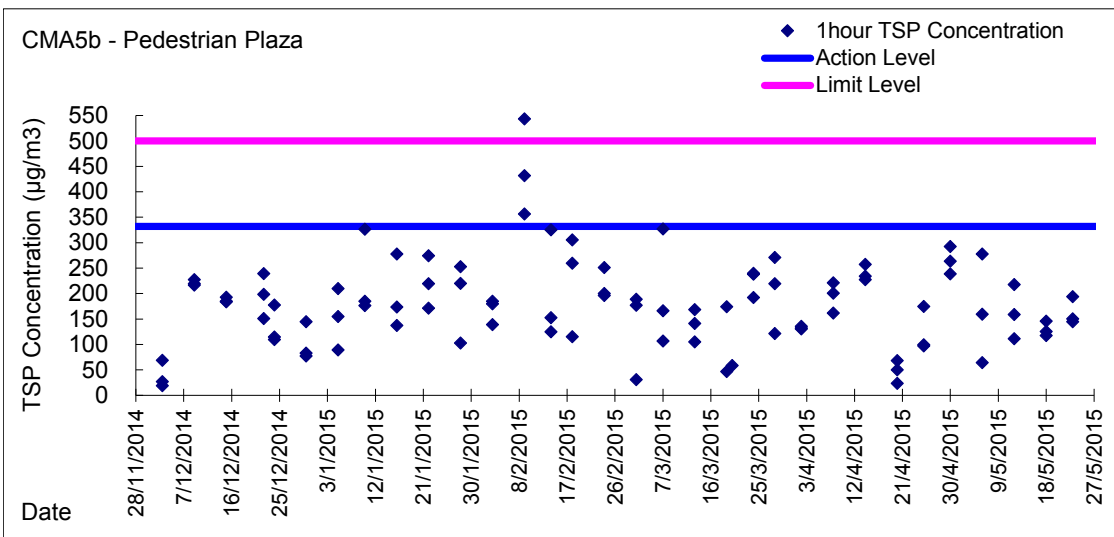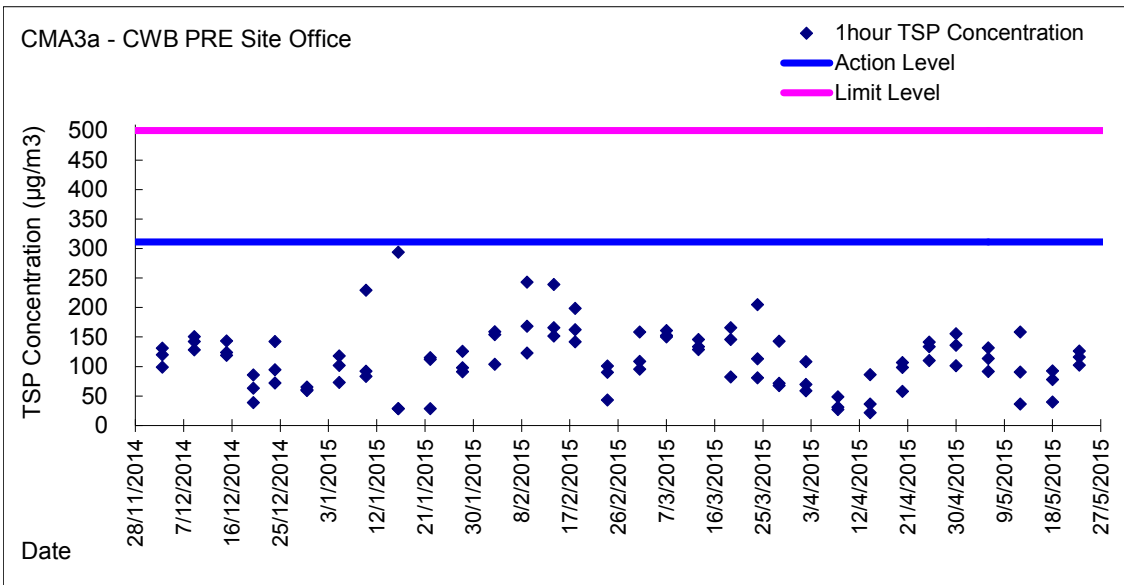Graphic Presentation of 1 hour TSP Result


Graphic Presentation of 24 hour TSP Result

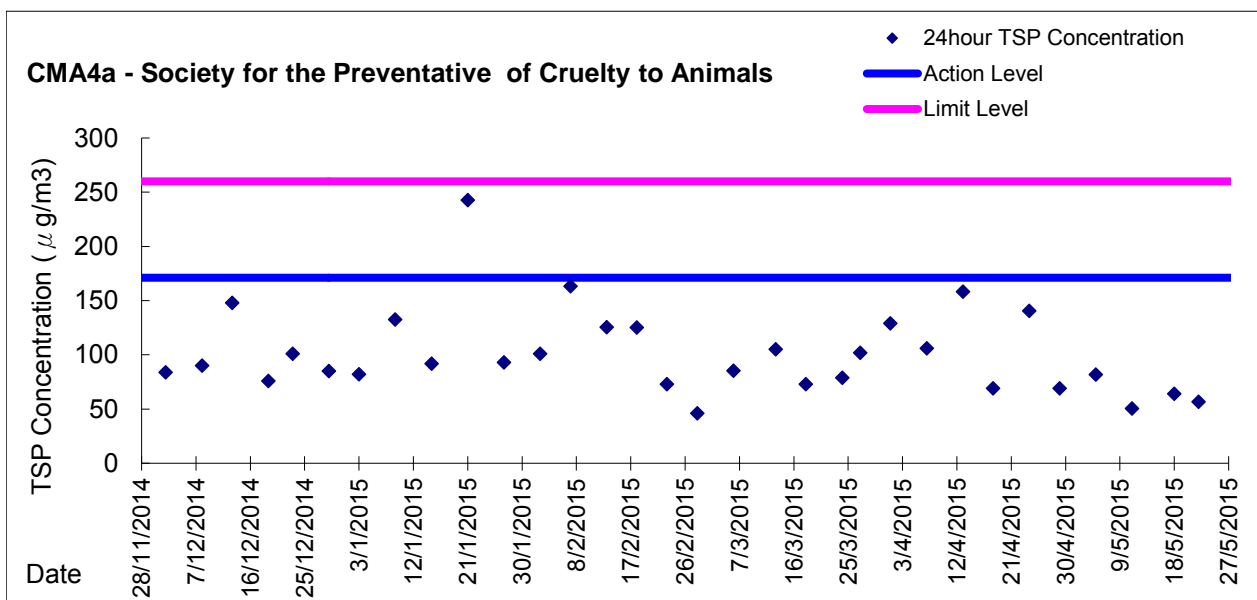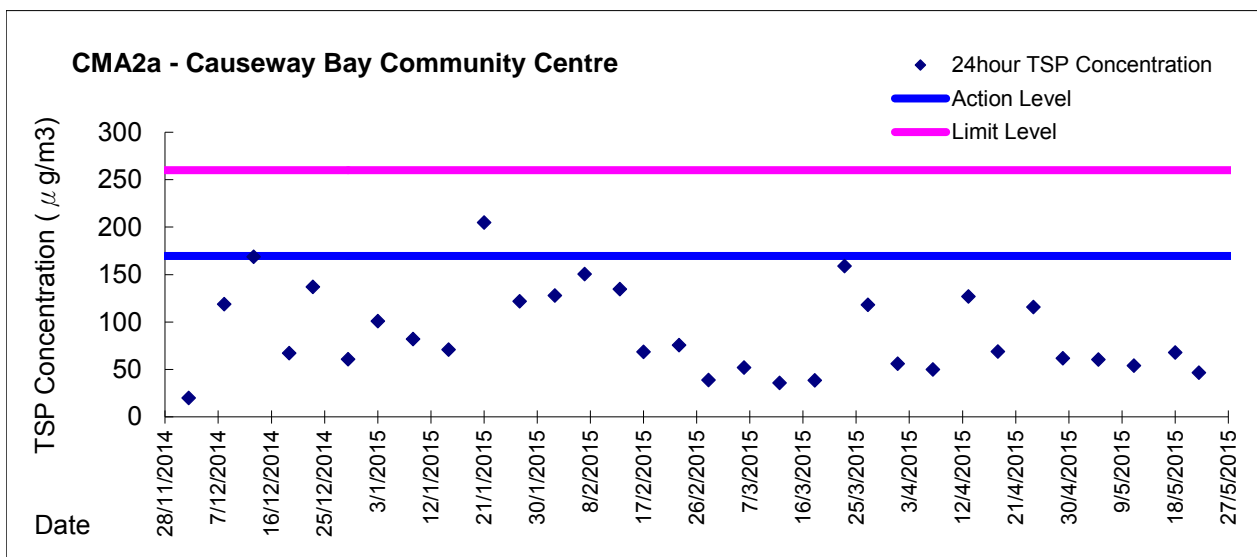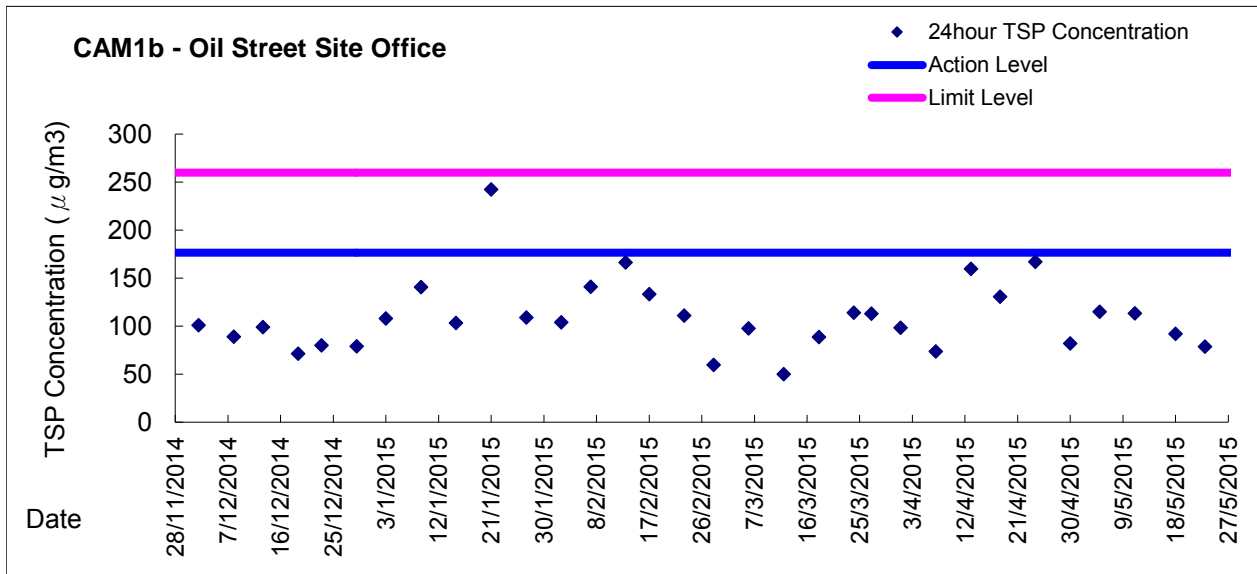

Graphic Presentation of 24 hour TSP Result

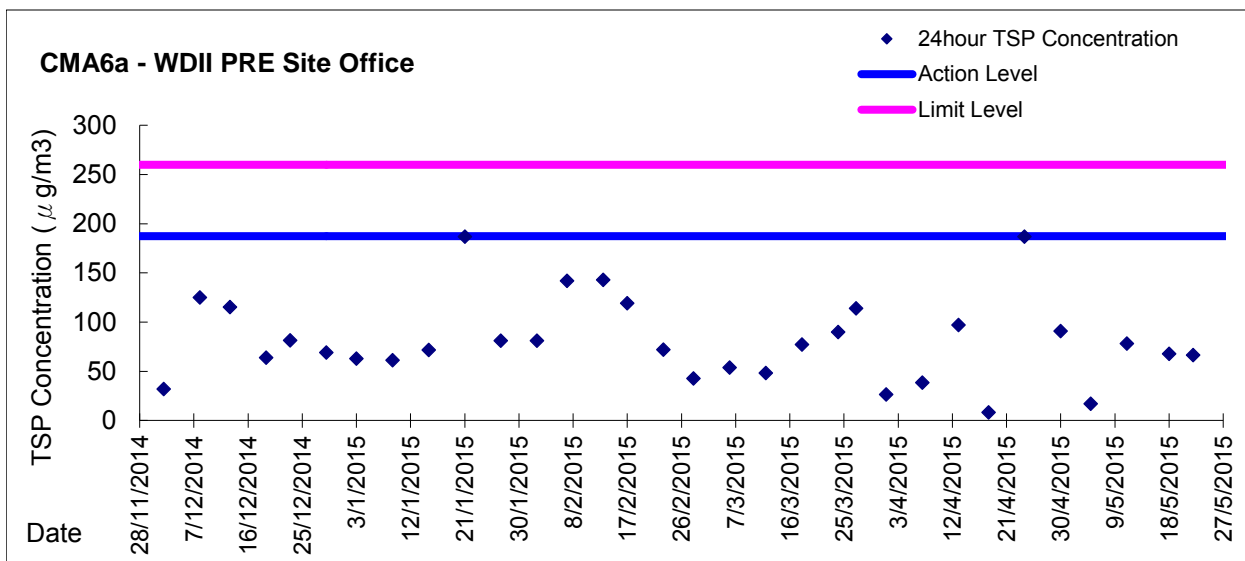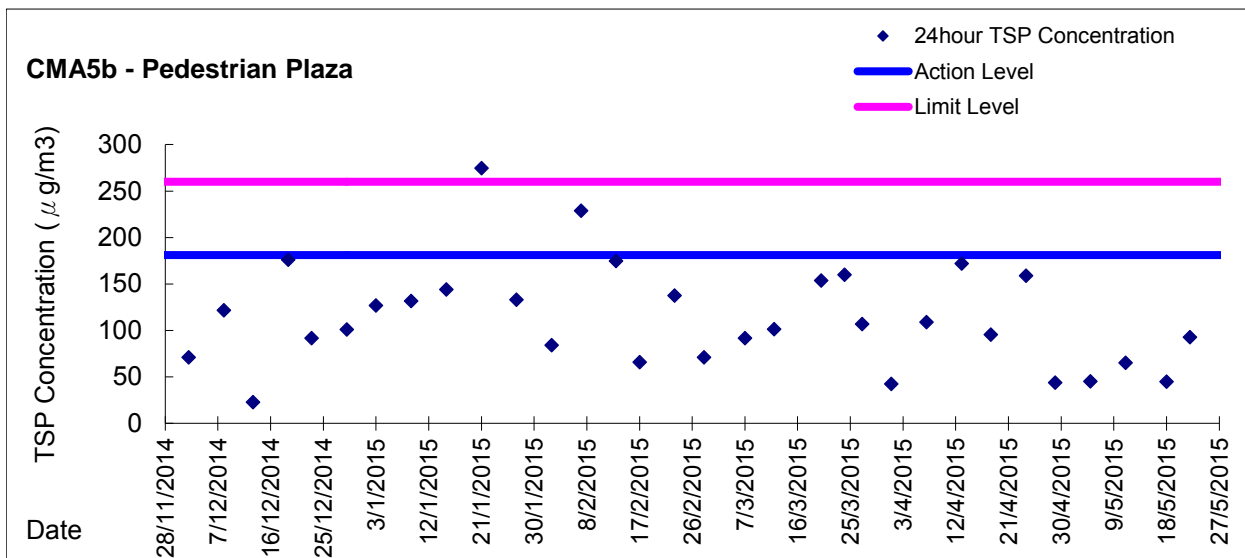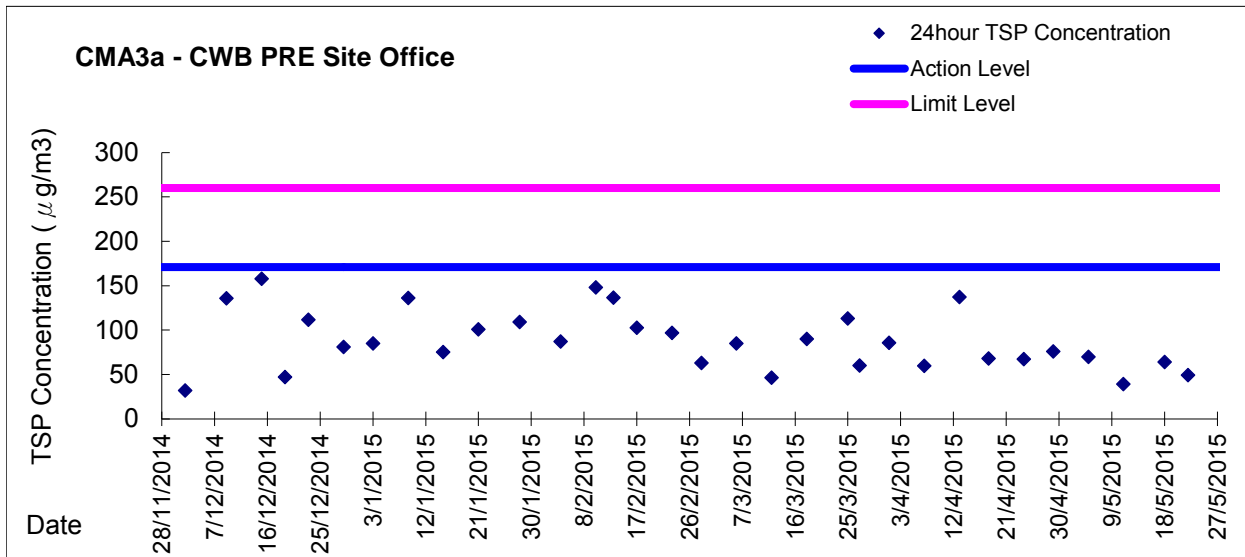






Appendix 4.3


Water Quality Monitoring Graphical Presentations



Graphic Presentation of Water Quality Result of WSD19 - Sheung Wan

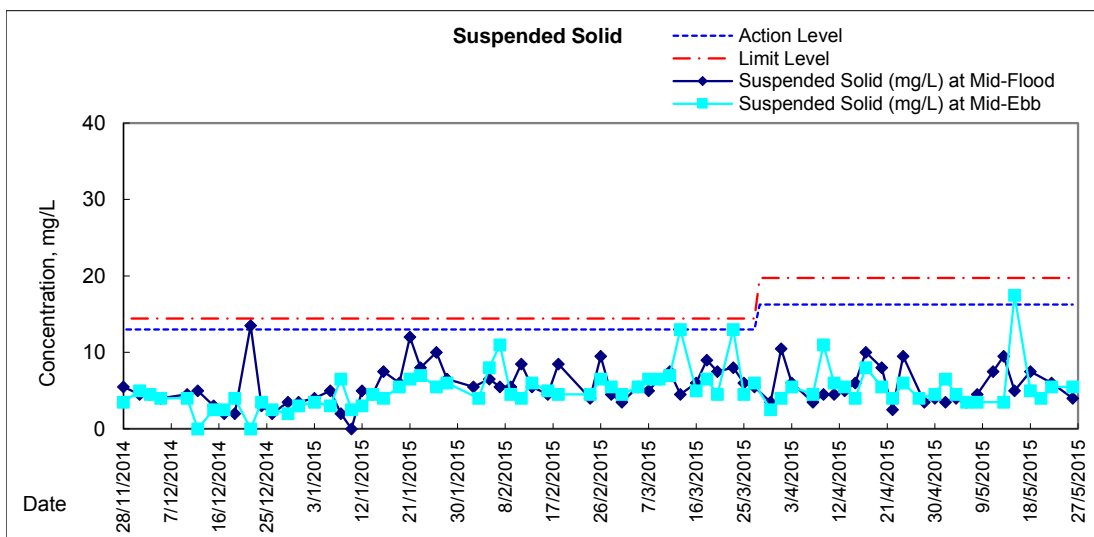
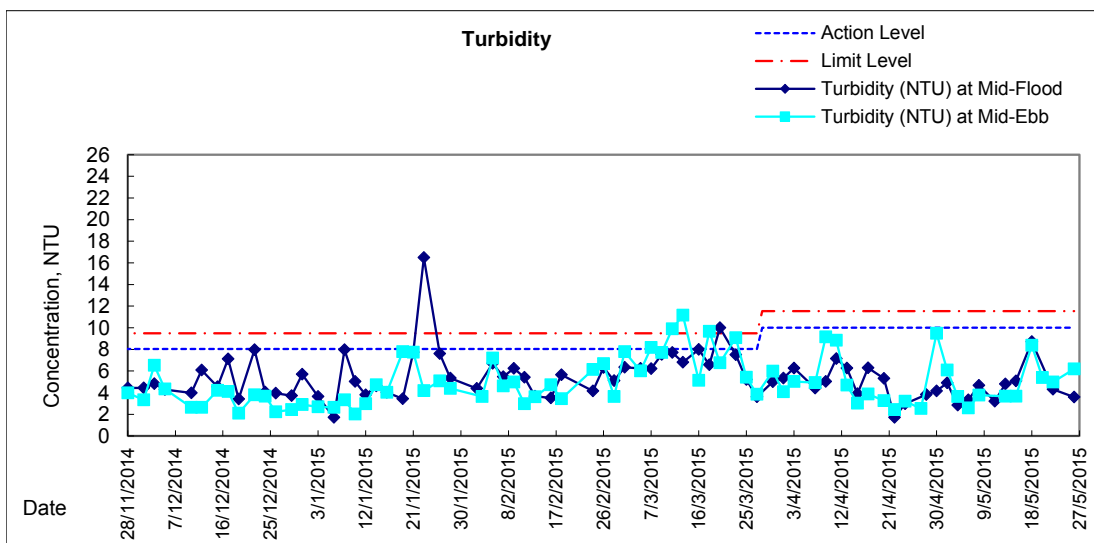
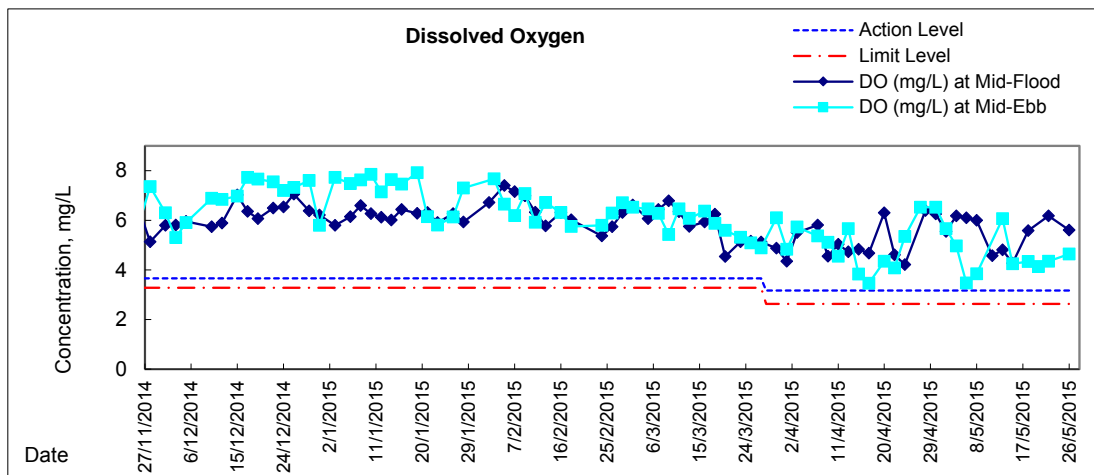


Graphic Presentation of Water Quality Result of C1 - HKCEC

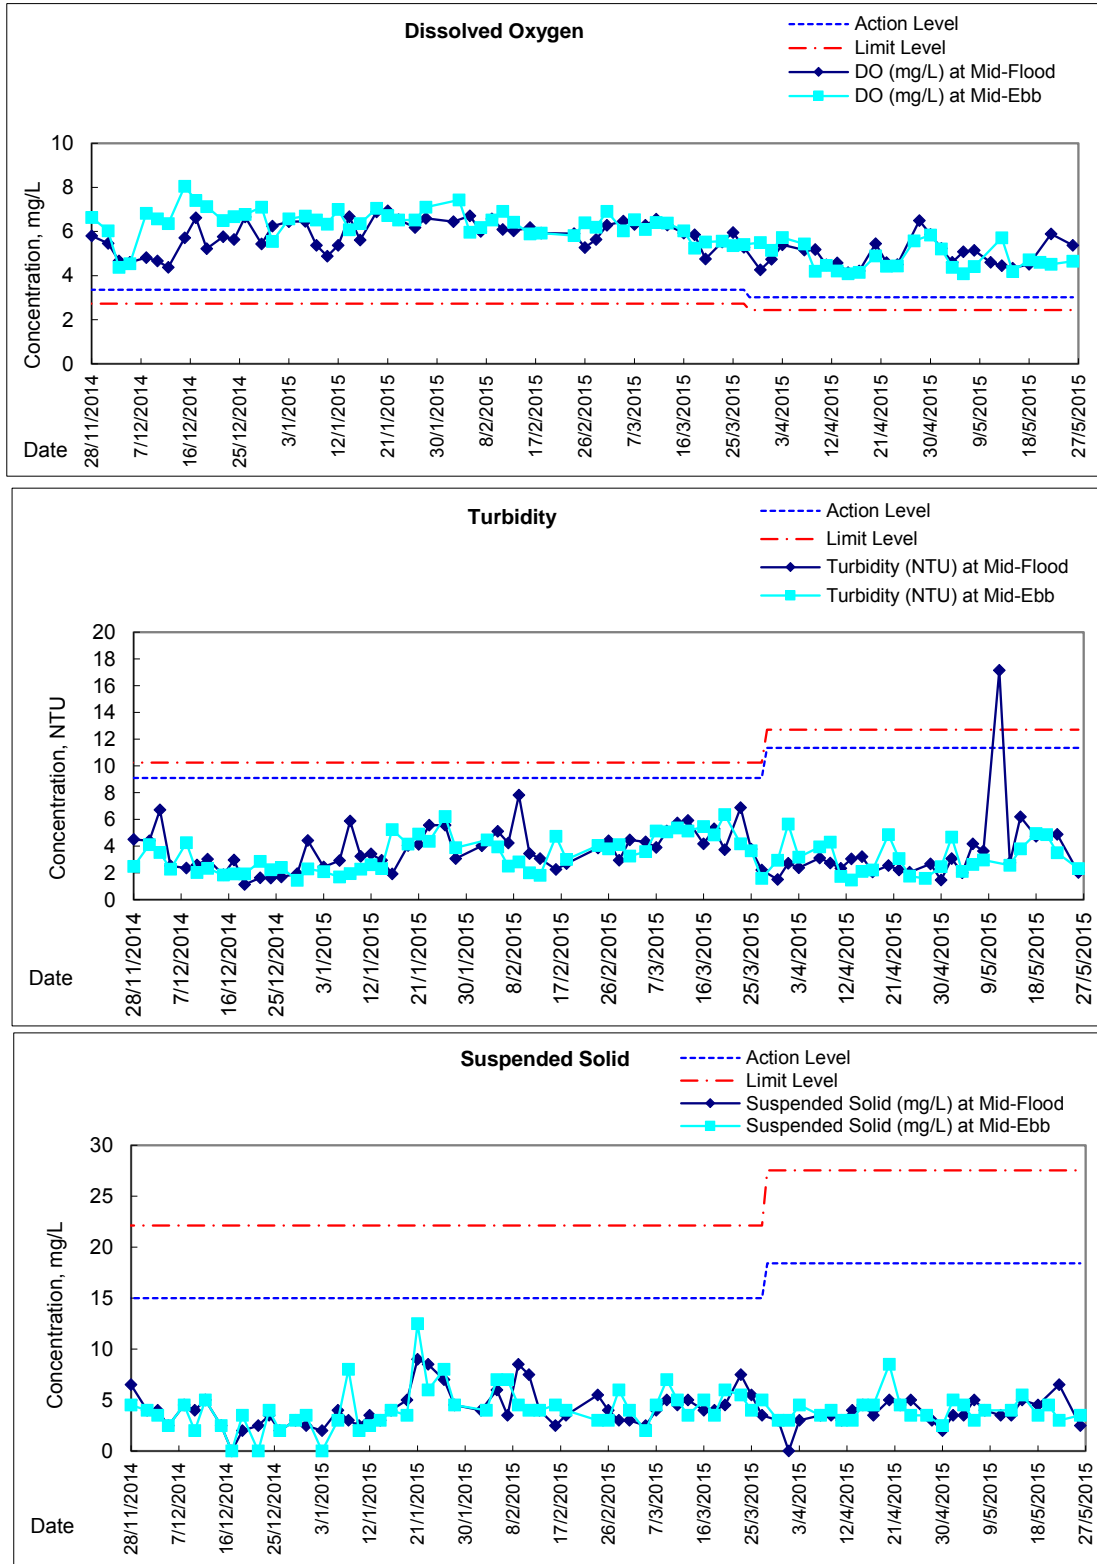






Graphic Presentation of Water Quality Result of P1 - HKCEC Phase I

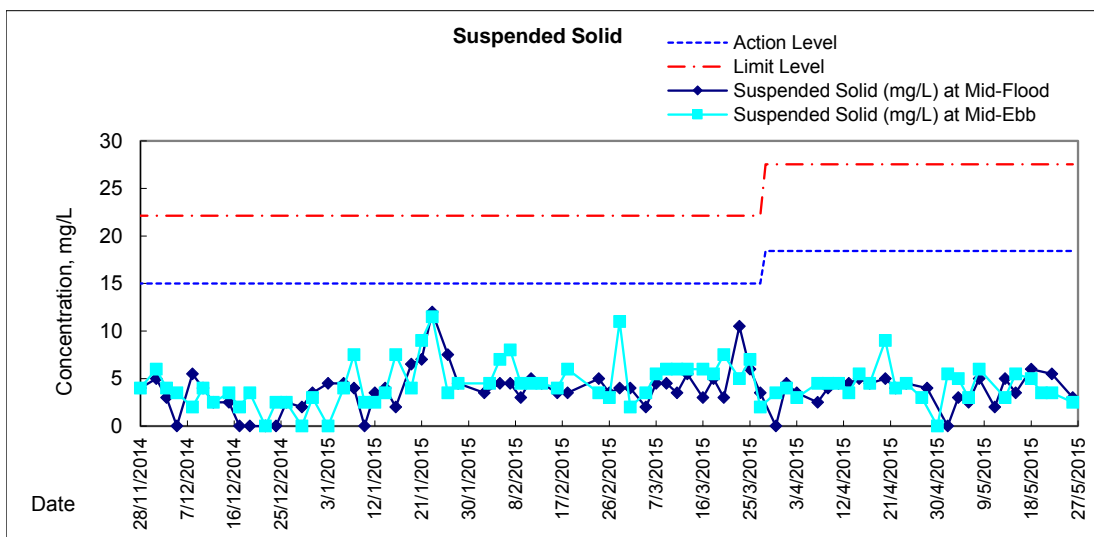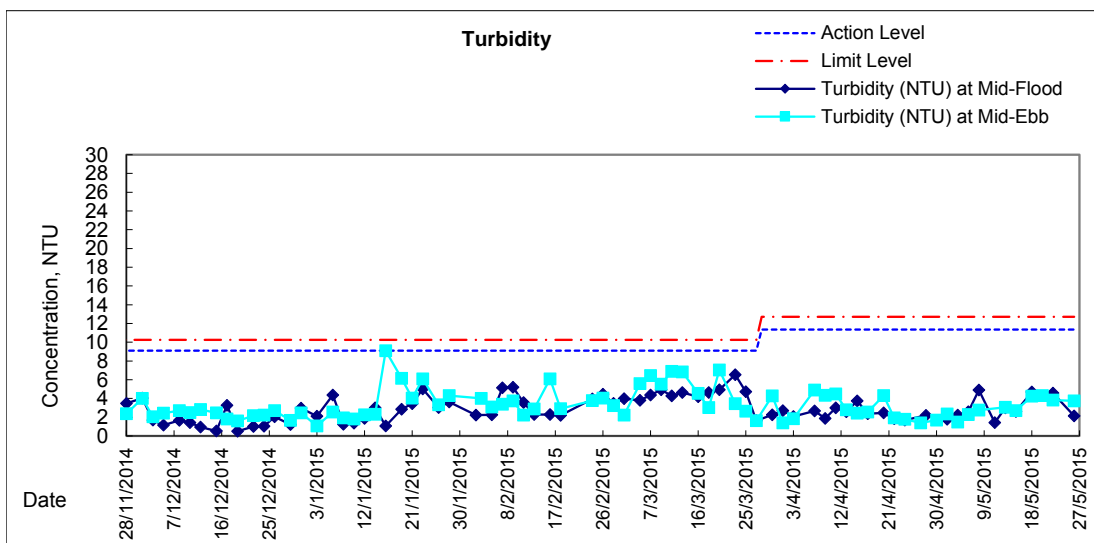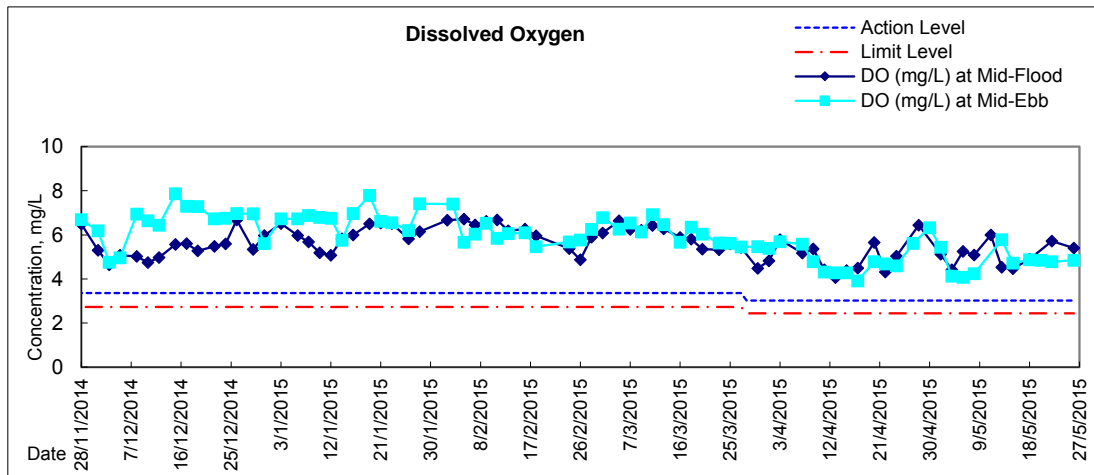






Graphic Presentation of Water Quality Result of P3 - APA

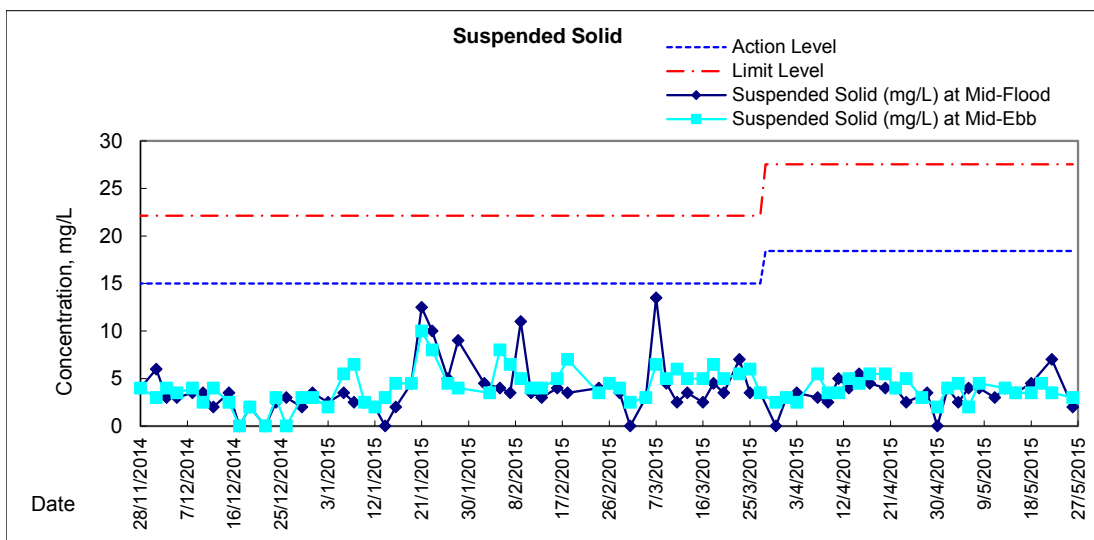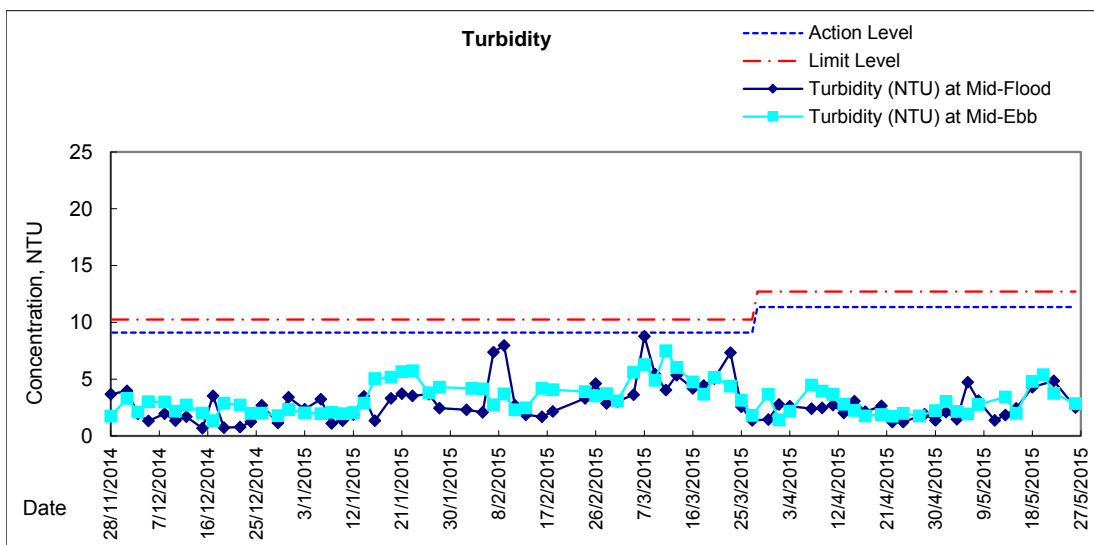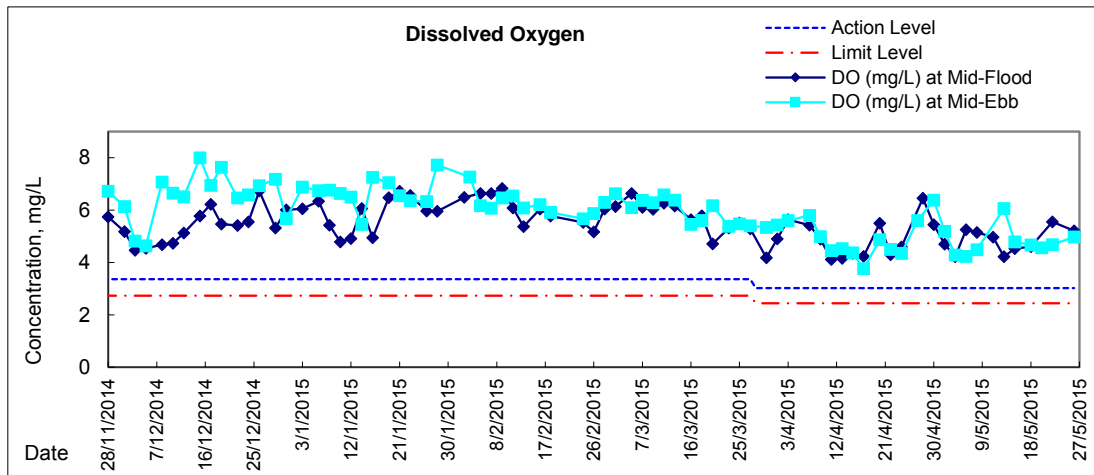






Graphic Presentation of Water Quality Result of P5 - WCT / RT / IT

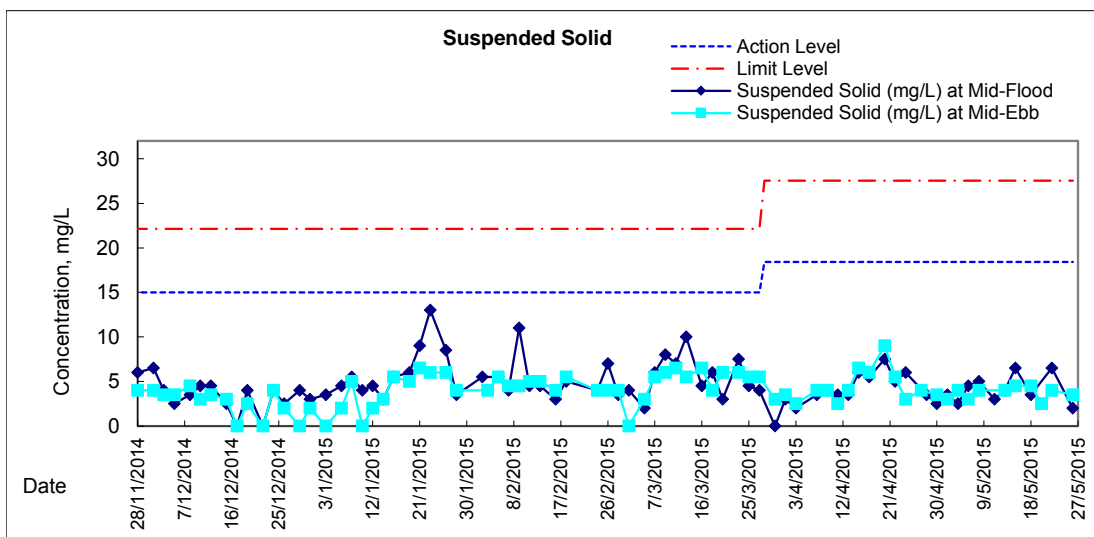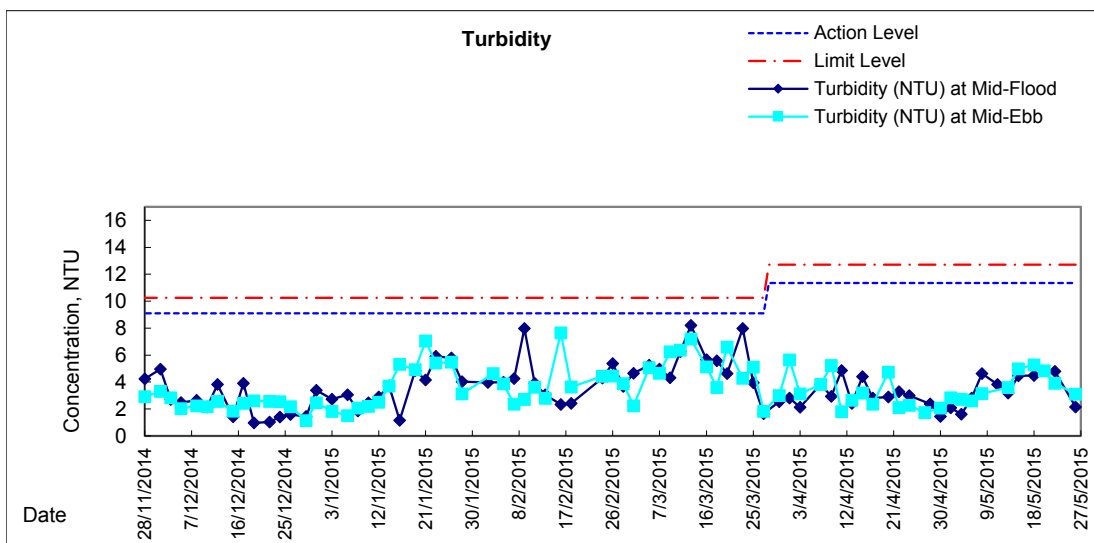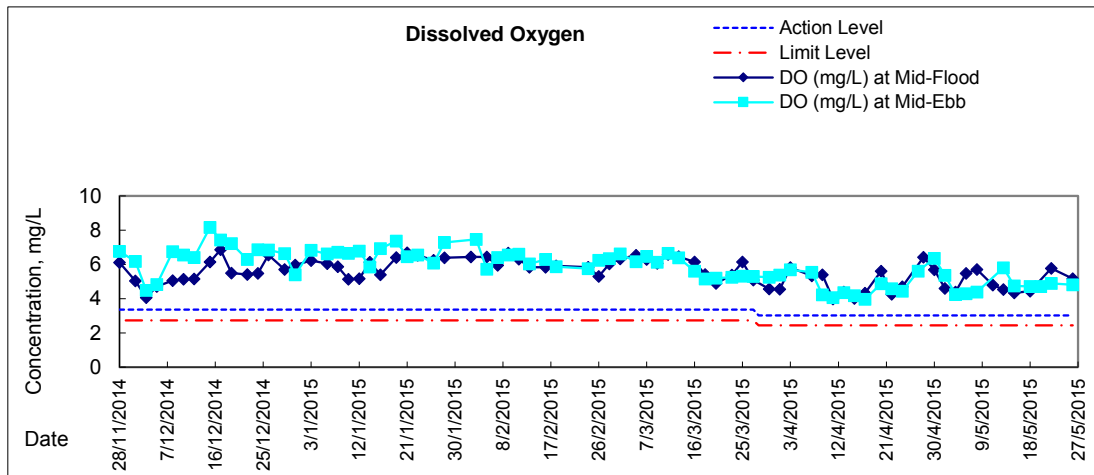






Graphic Presentation of Water Quality Result of P4 - SOC

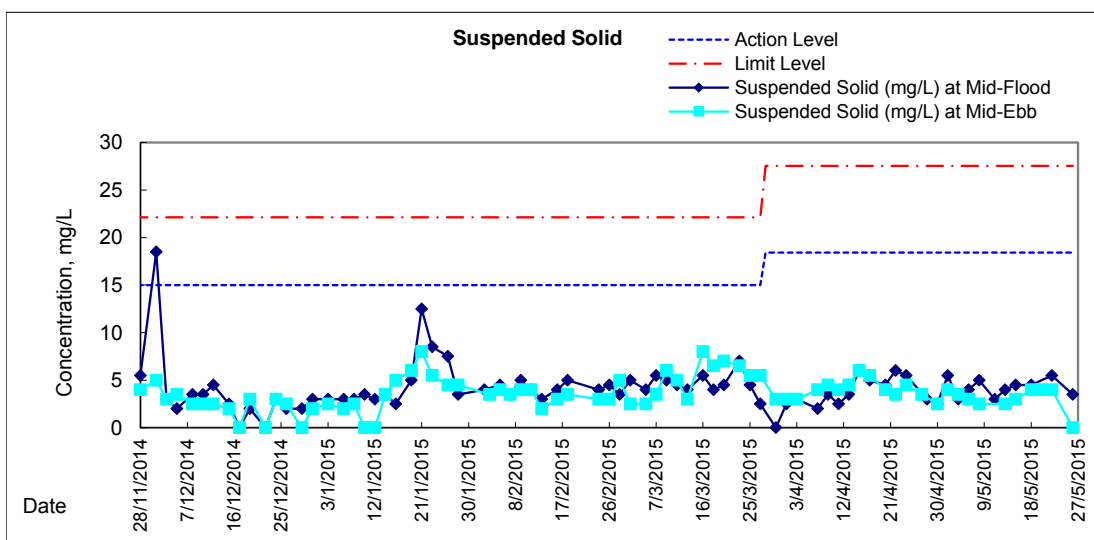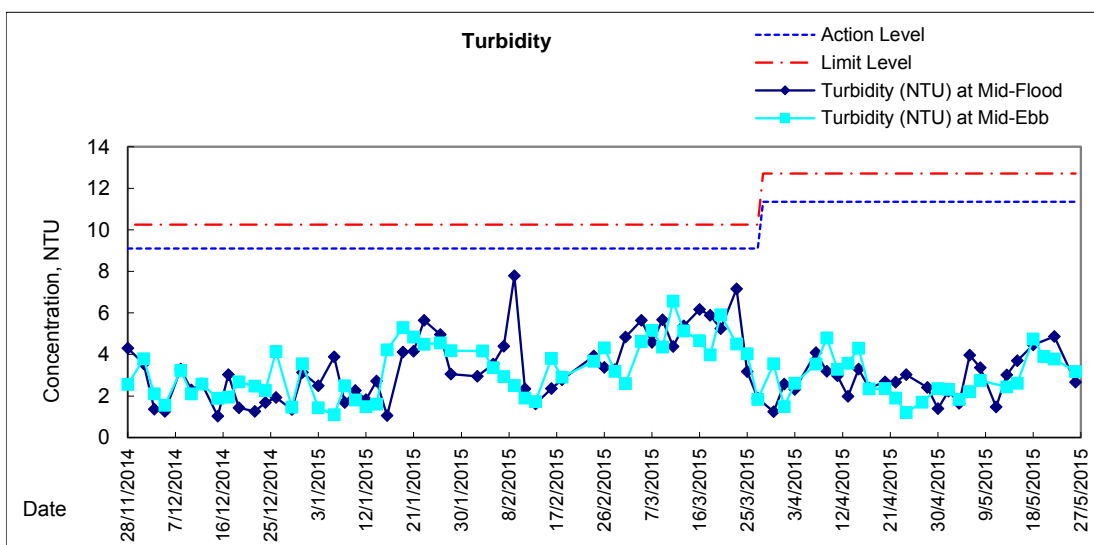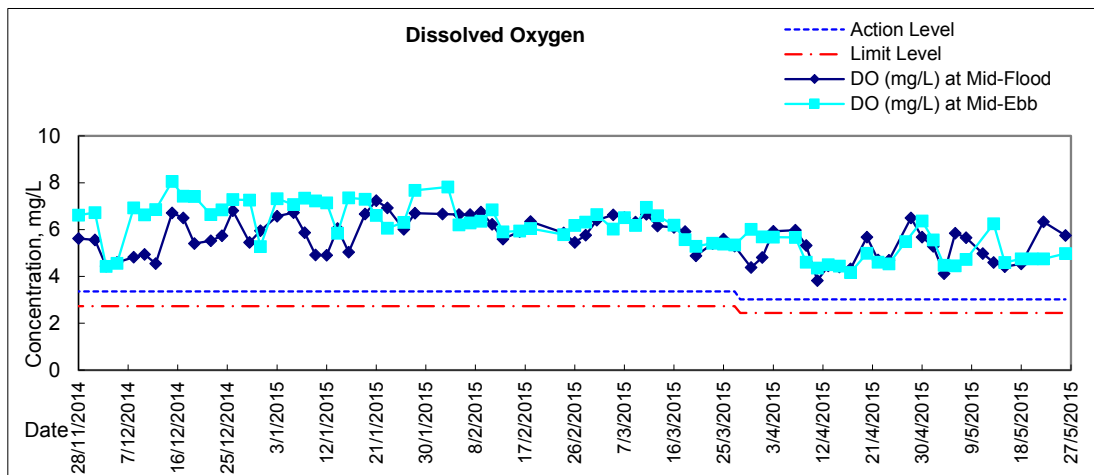






Graphic Presentation of Water Quality Result of RW21-P789 - GEC/CRC/SHK

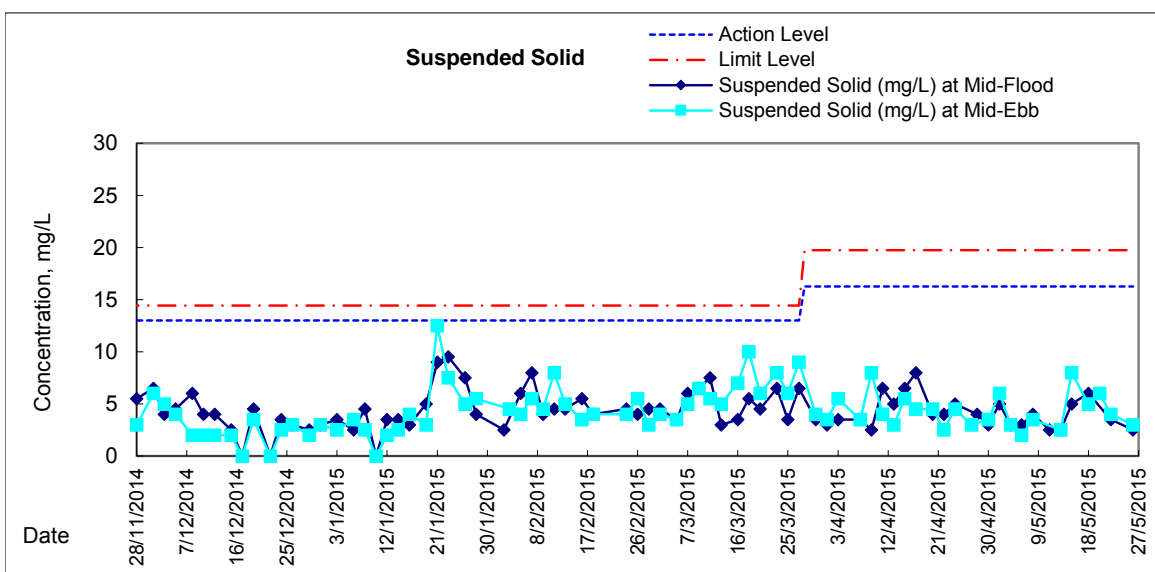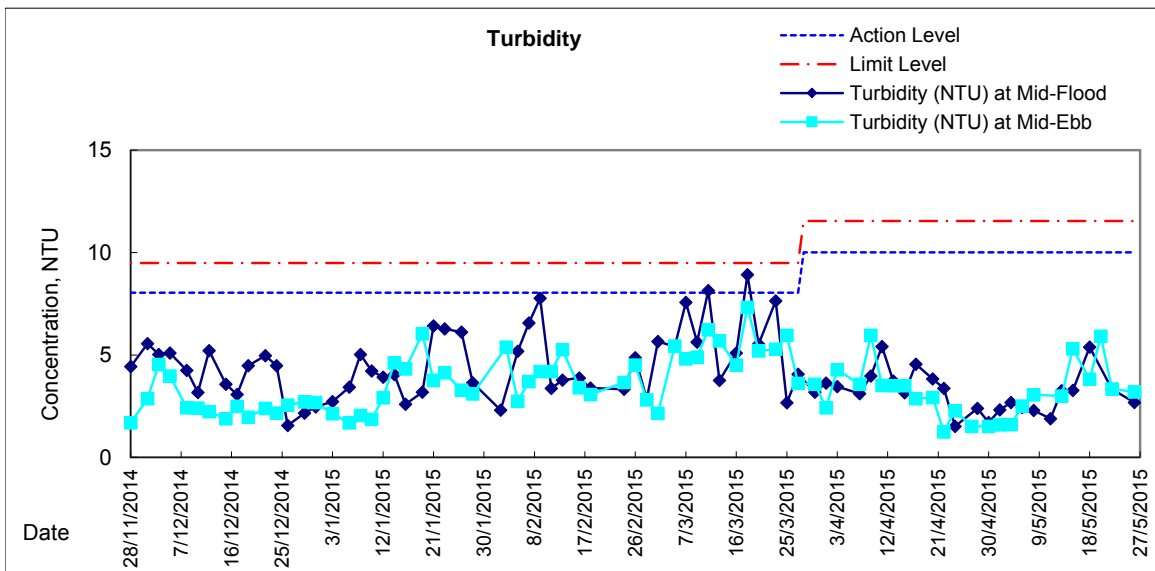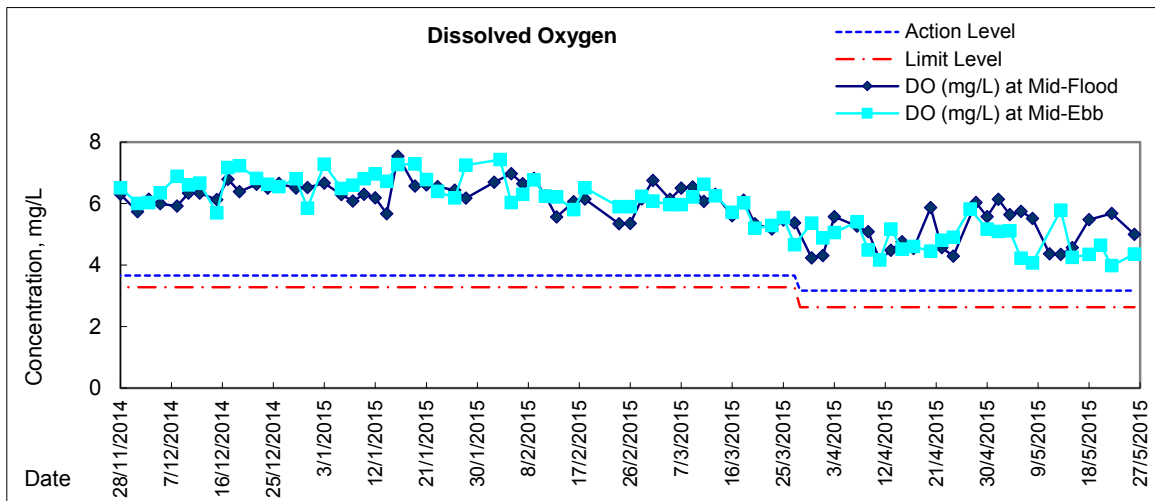





Graphic Presentation of Water Quality Result of C7 - Windsor House

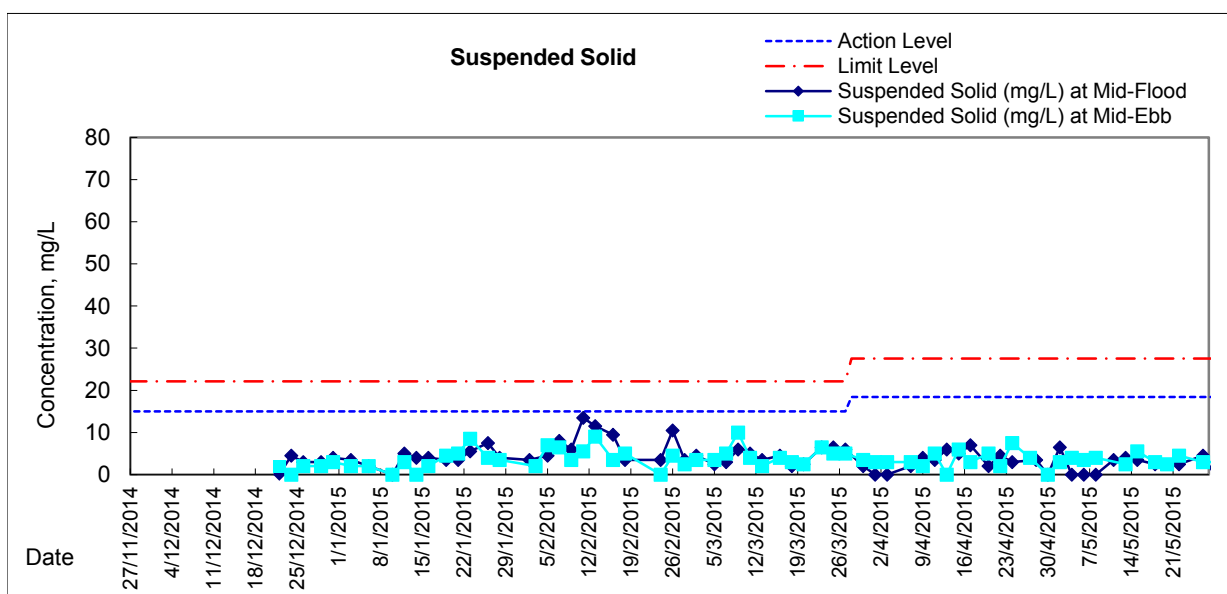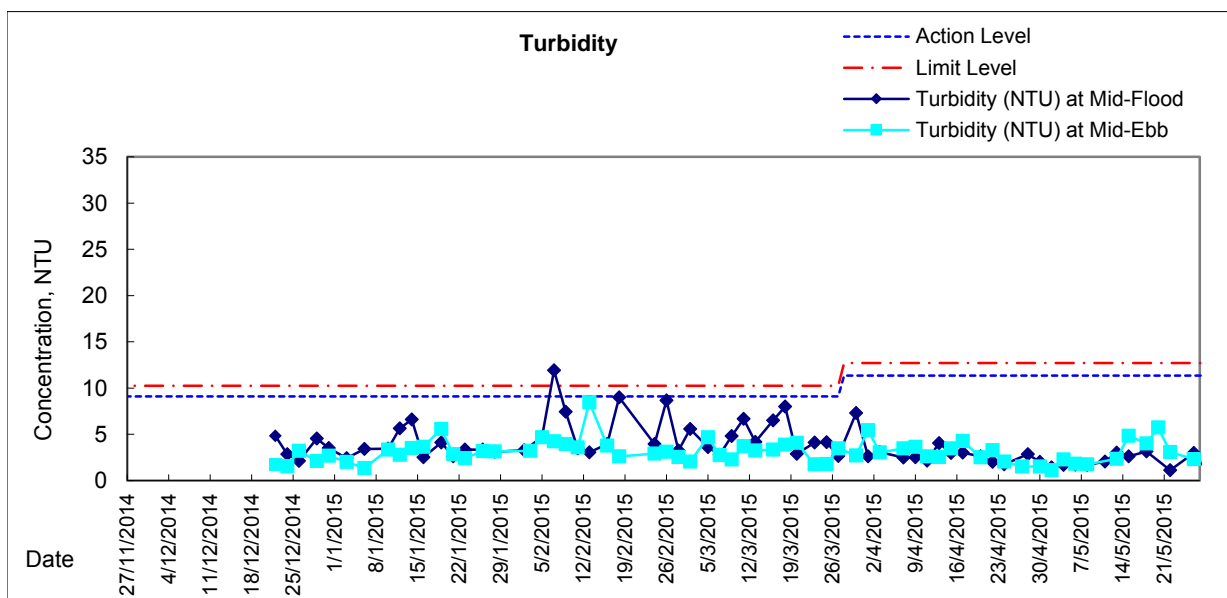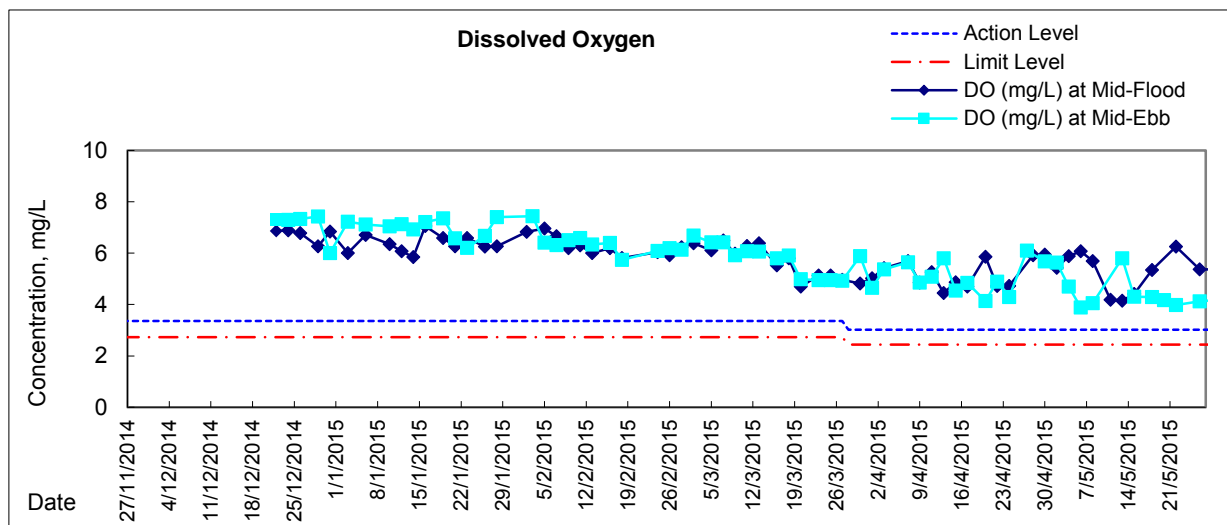





Graphic Presentation of Enhanced Water Monitoring Results (DO) at C6 - Excelsior Hotel

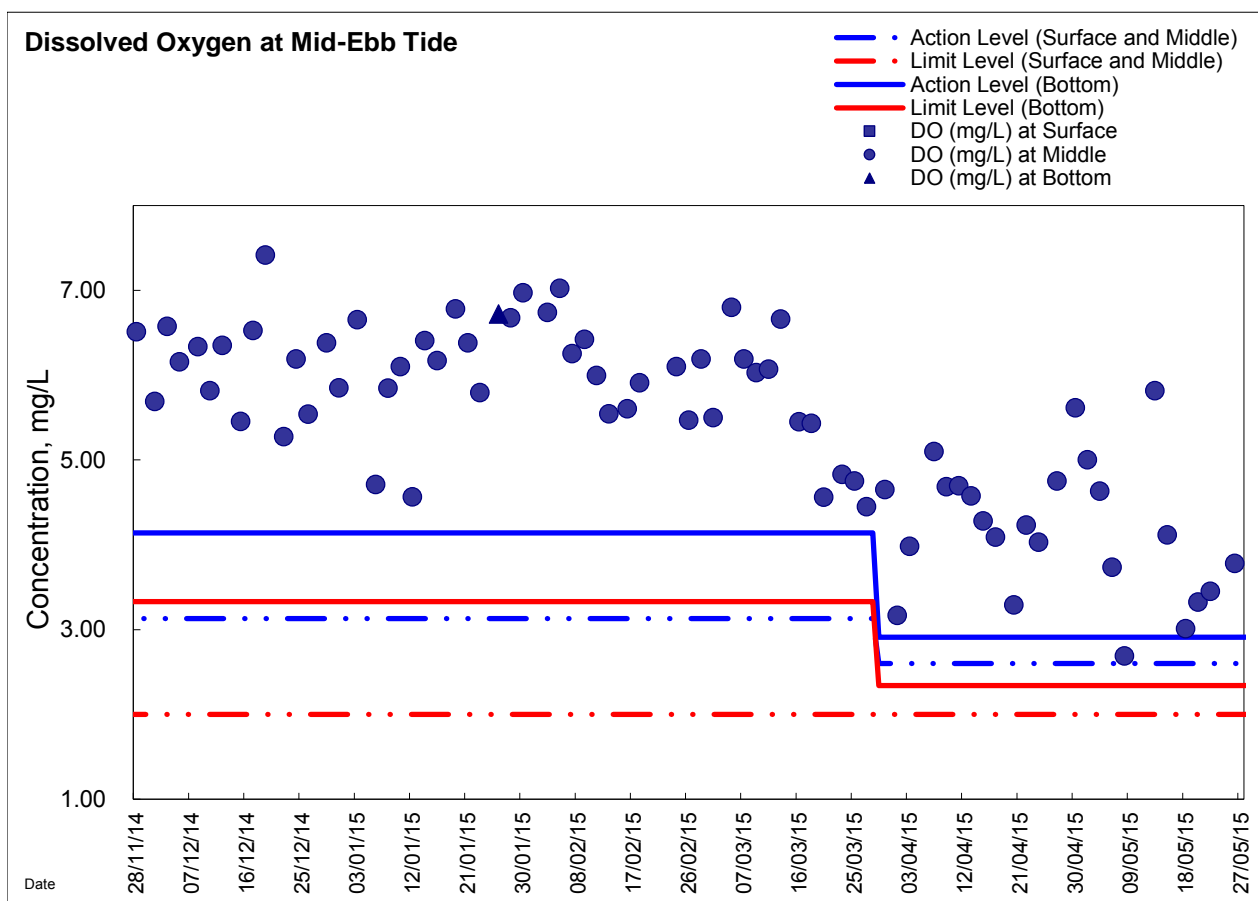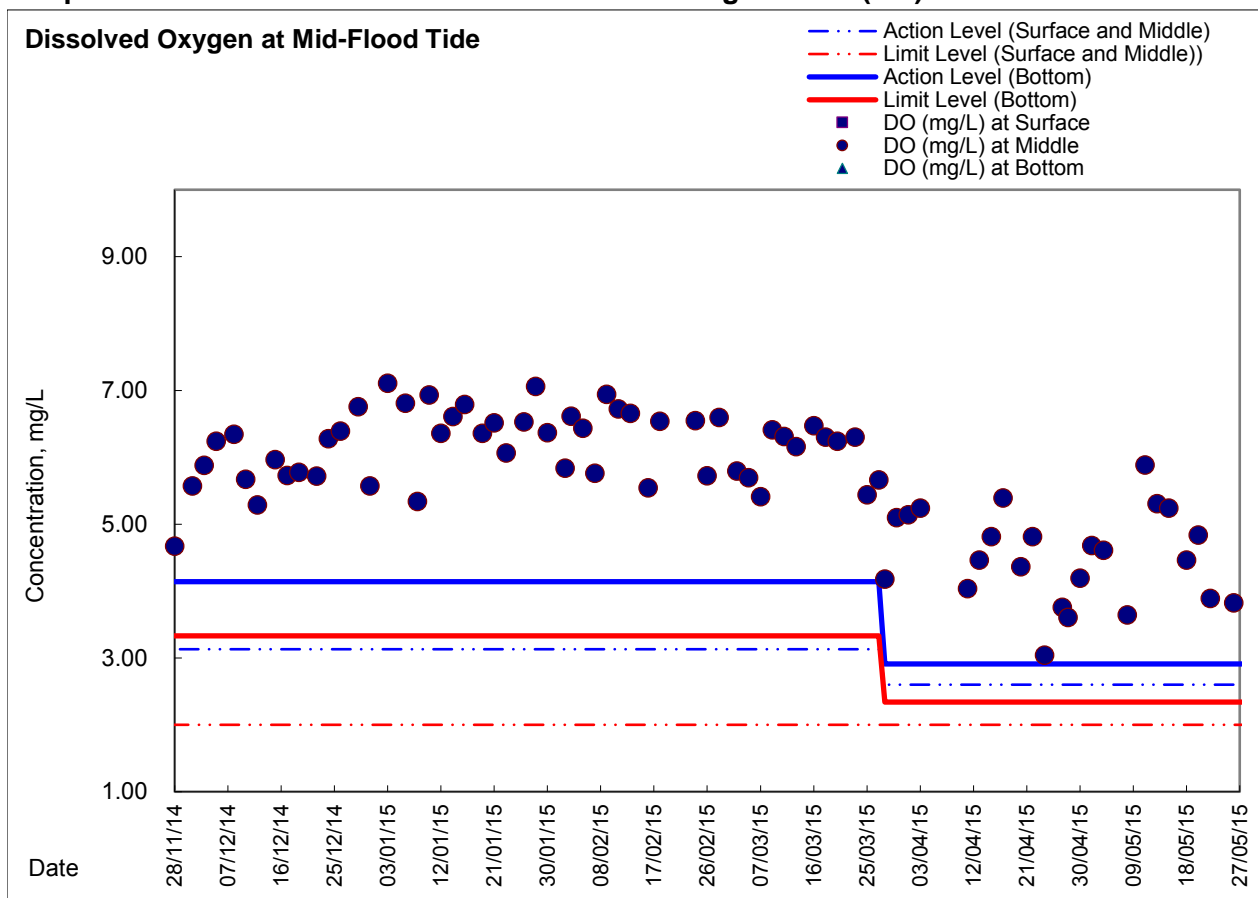





Graphic Presentation of Enhanced Water Monitoring Results (DO) at Ex-WPCWA SW
- South-western corners of ex-Public Cargo Works Area

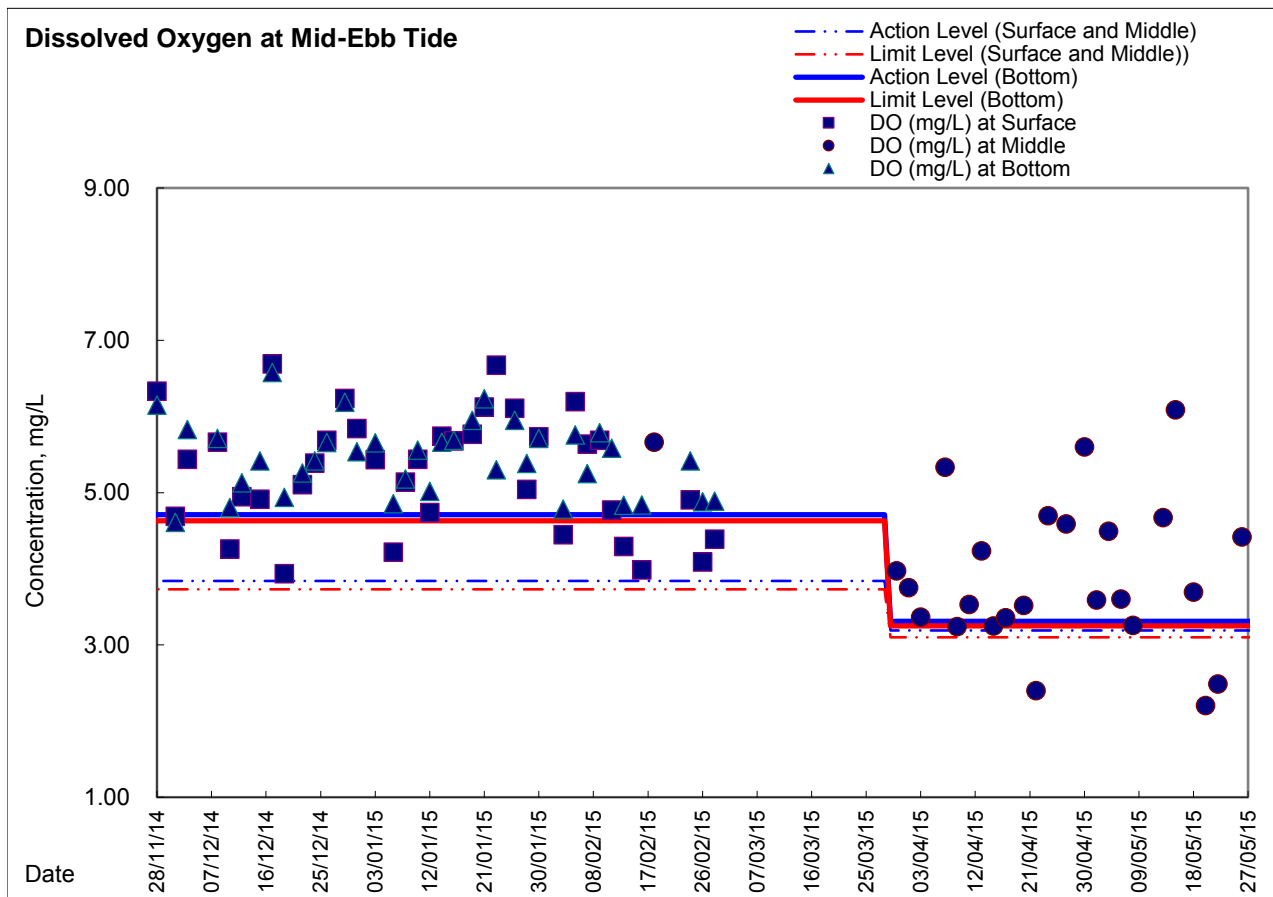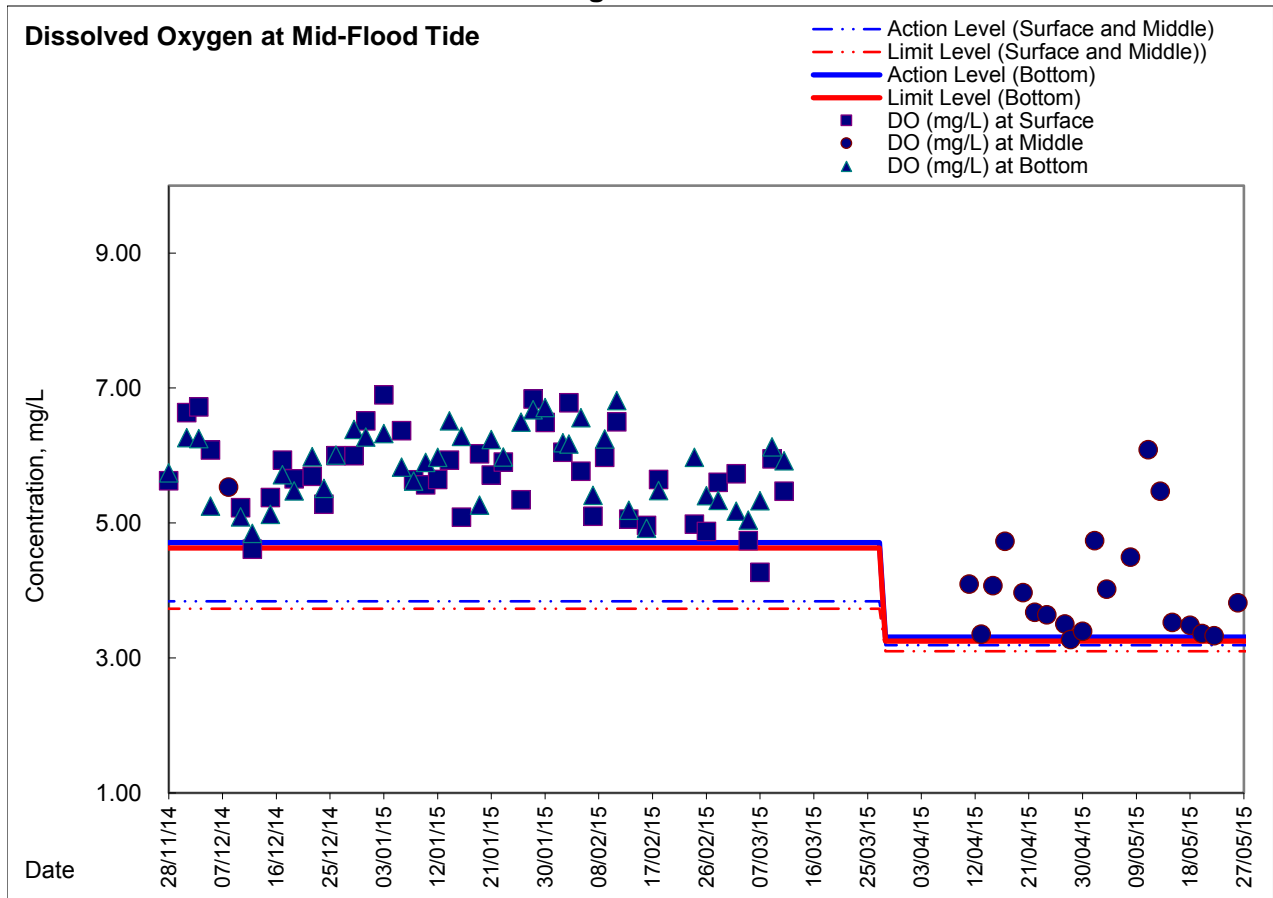



Graphic Presentation of Enhanced Water Monitoring Results (DO) at Ex-WPCWA SE
- South-eastern corners of ex-Public Cargo Works Area

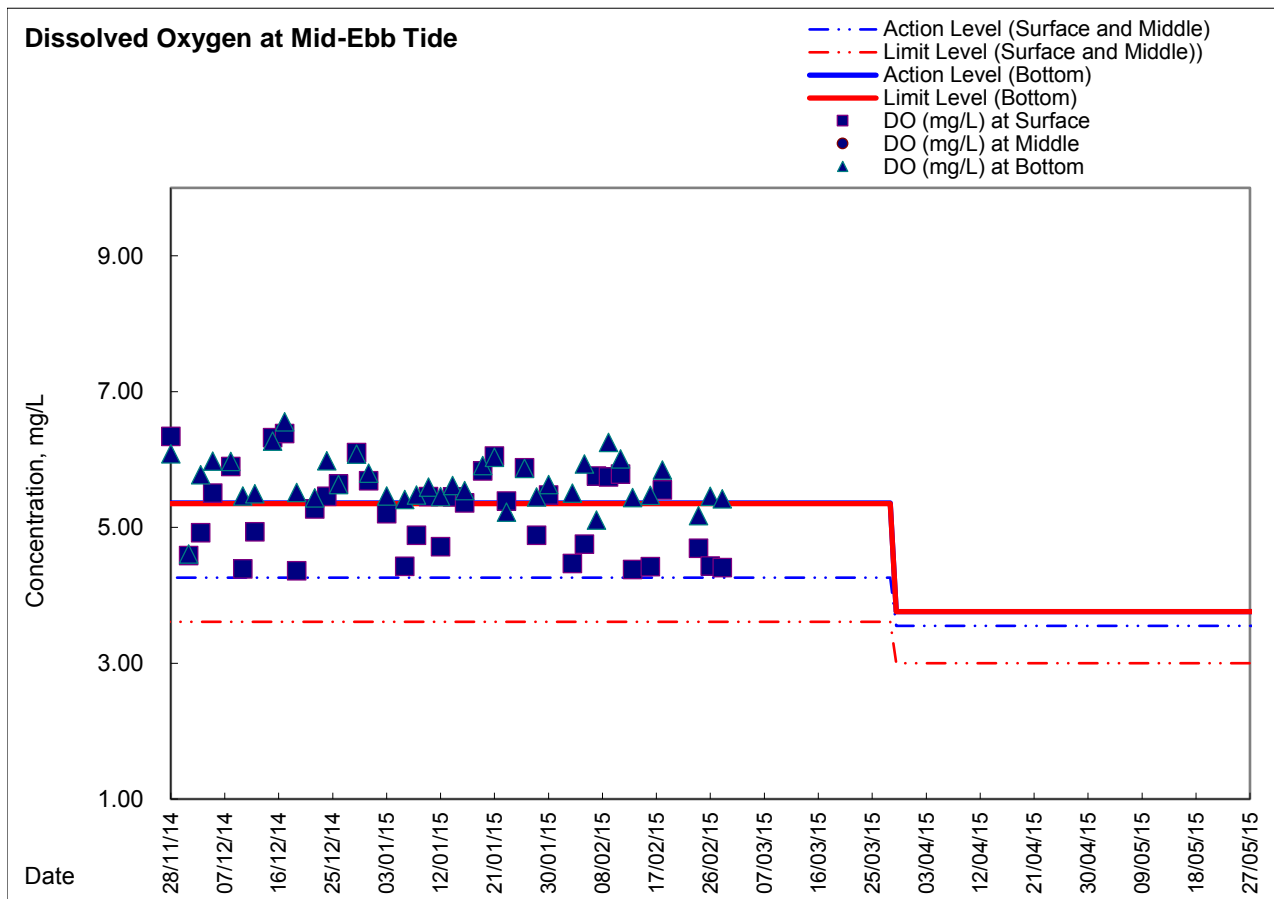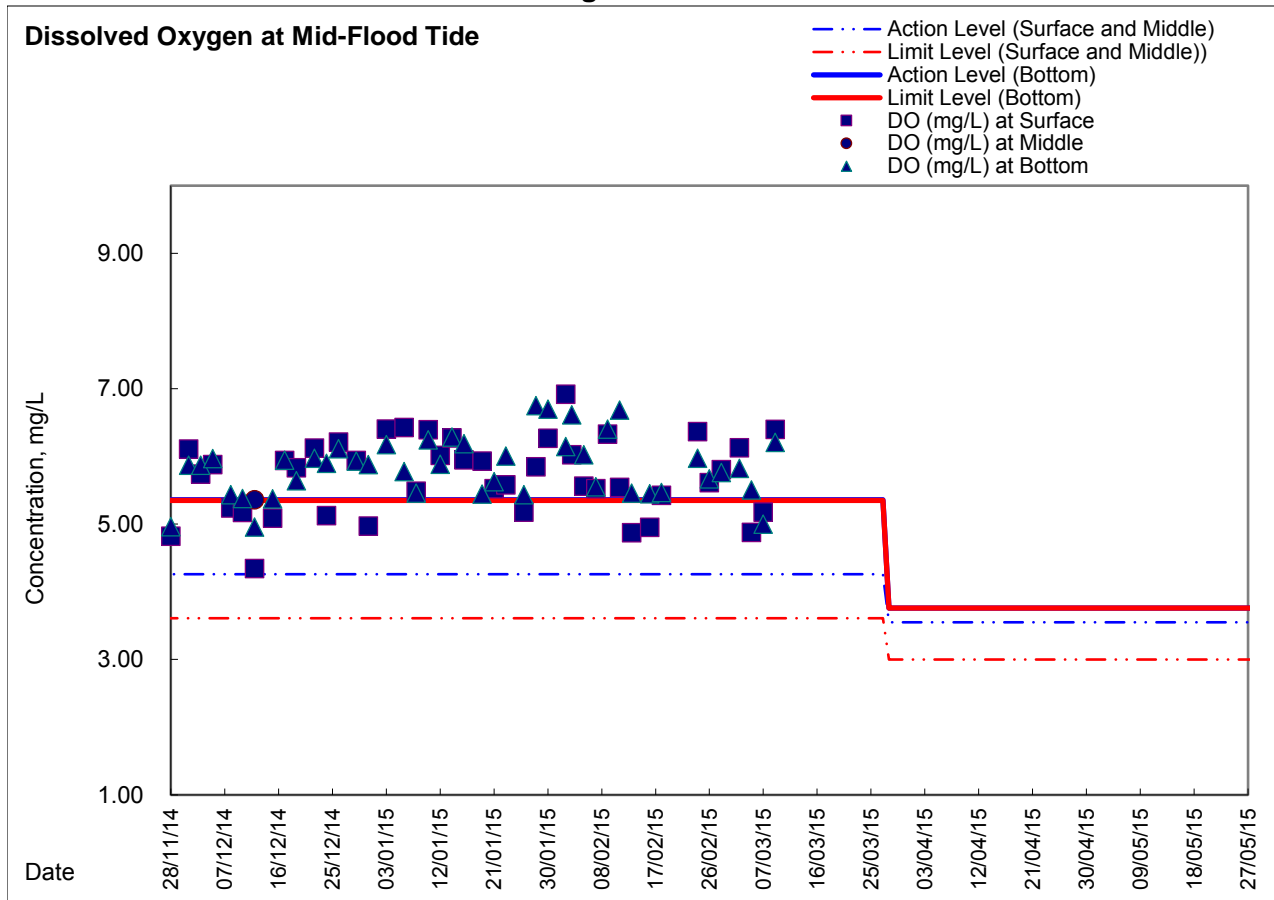




Appendix 4.4


Real-time Noise Monitoring Results and Graphical Presentations

Graphic Presentation of Real Time Noise Monitoring Result (RTN2a- Hong Kong Electric Centre)

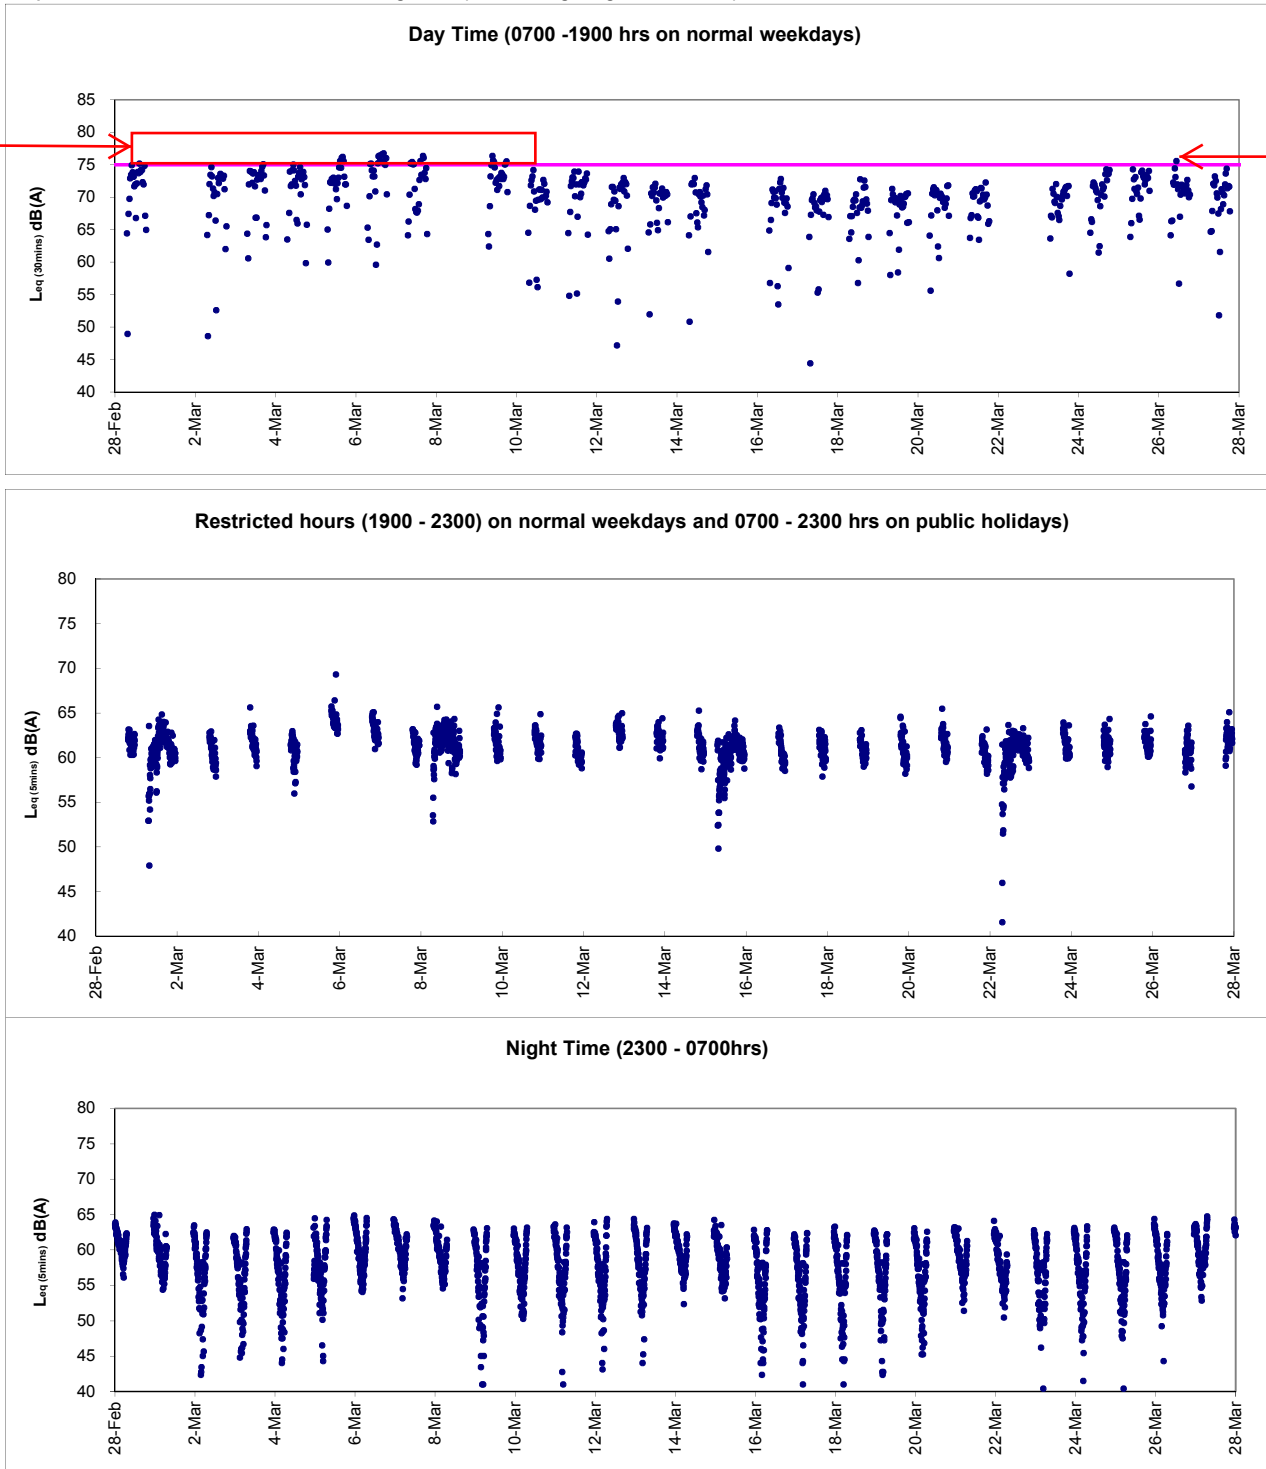


After checking with Contractor HY/2009/19, trench excavation and sheet piling works were undertaken at the concerned location during the recorded period and noise mitigation measures including erection of noise blanket was implemented by the Contractor. Meanwhile, breaking works and excavation works was observed at the non-CWB Project construction site next to the monitoring station across March 2015 and considered as the major noise contribution and as such, the exceedances were considered to be non Project related and contributed by nearby non-CWB Project construction works.

Graphic Presentation of Real Time Noise Monitoring Result (RTN2a- Hong Kong Electric Centre)

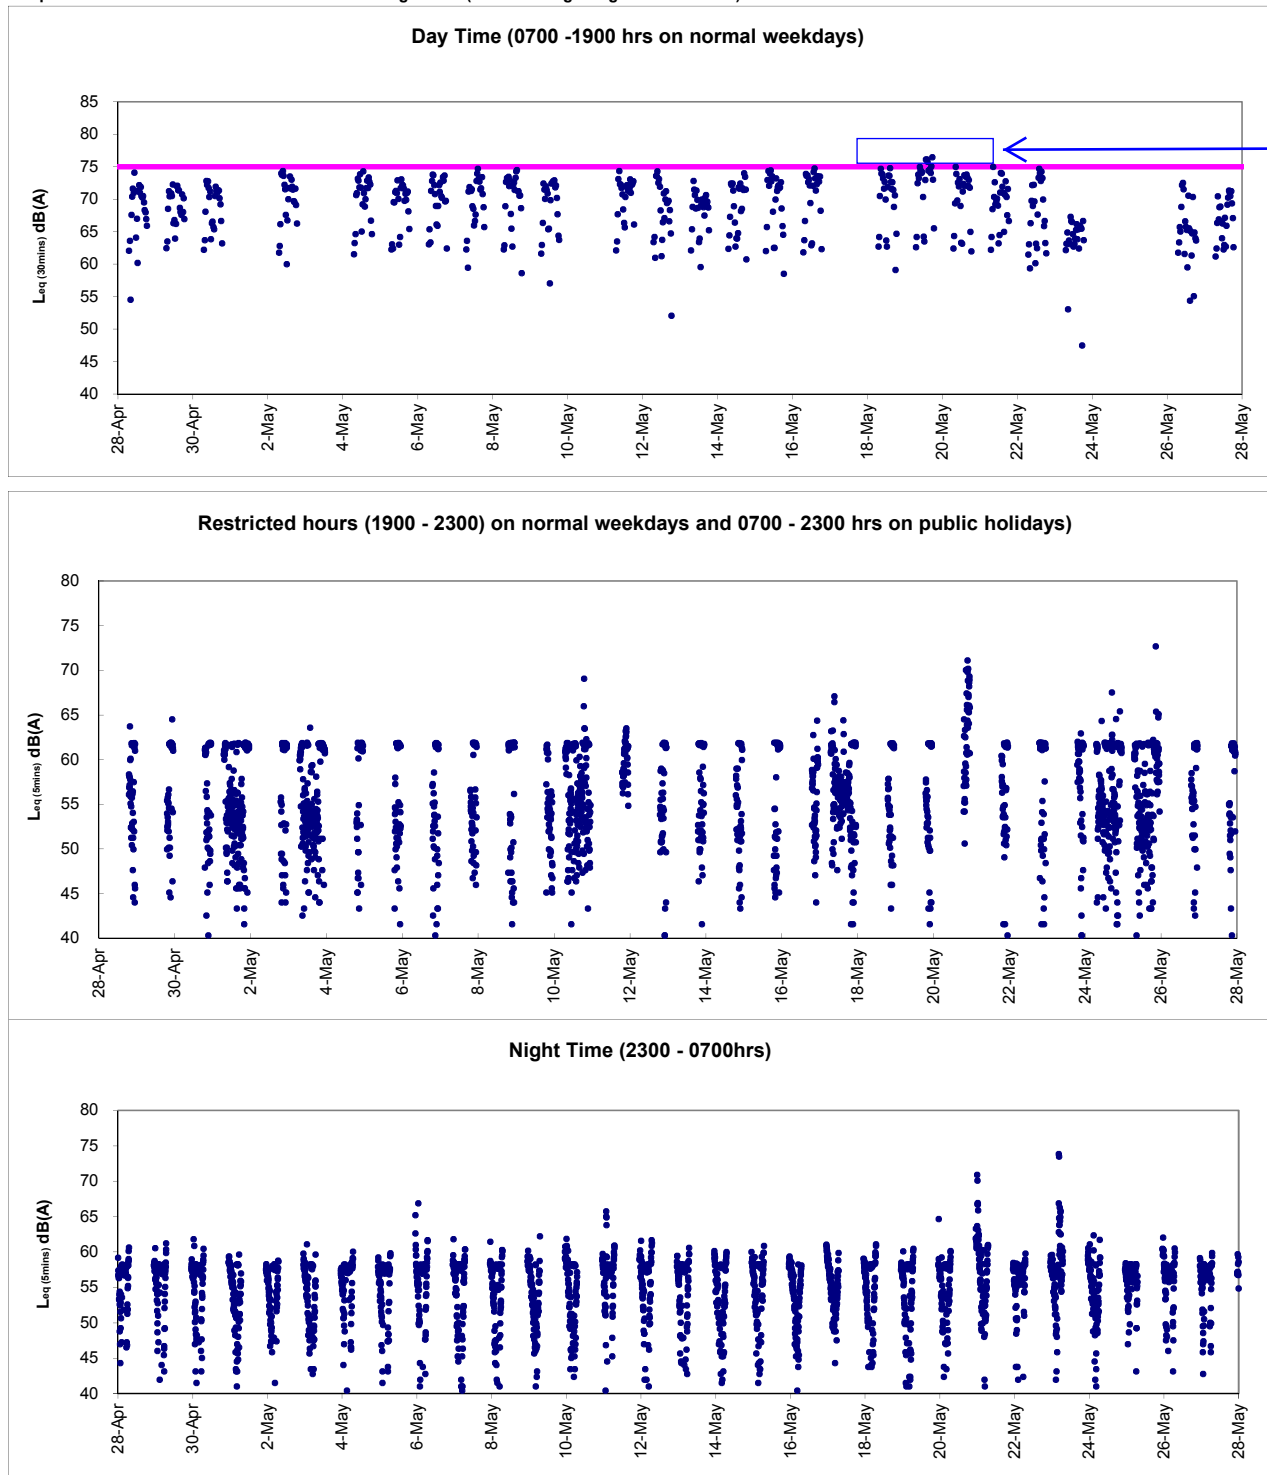

After checking with Contractor of HY/2009/19, U beam lifting works with trailer trucks and crawler crane was conducted on 19 May 2015 and Noise mitigation measures including erection of noise blanket was implemented by the Contractor while breaking works and excavation works was noted on-going at the construction site located next to the monitoring station. In view of the above, the exceedances were considered to be non-Project related and contributed by nearby non-CWB construction site works.

Graphic Presentation of Real Time Noise Monitoring Result (RTN2a- Hong Kong Electric Centre)

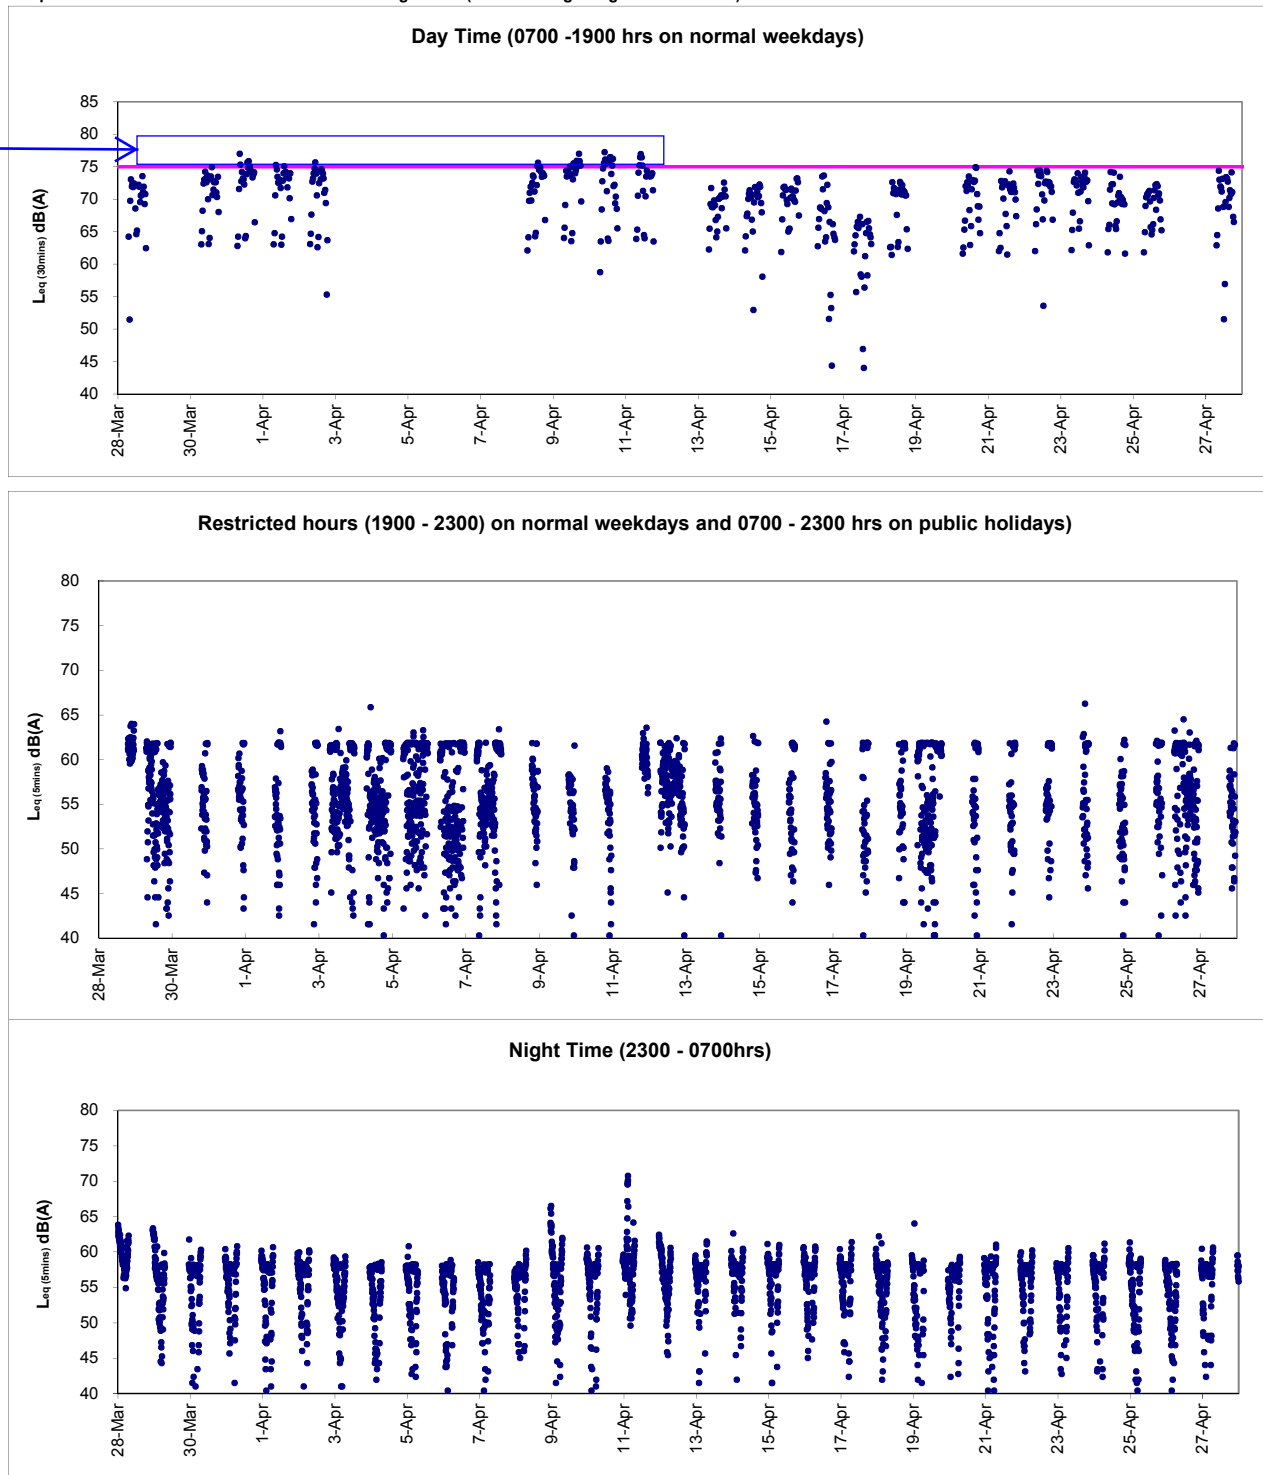

After checking with Contractor of HY/2009/19, sheet-pile driving works were conducted on 31 March 2015 and 2 April 2015 while sheet-pile extraction works were conducted on 8, 9, 10 and 11 April 2015. Noise mitigation measures including erection of noise blanket was implemented by the Contractor while breaking works and excavation works were observed across the concerned period at the construction site located next to the monitoring station. In view of the above, the exceedances were considered to be non-Project related and contributed by nearby non-CWB construction site works..



Appendix 5.1

Event Action Plans



Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	<ol style="list-style-type: none">1. Notify ER, IEC and Contractor;2. Carry out investigation;3. Report the results of investigation to the IEC, ER and Contractor;4. Discuss with the IEC and Contractor on remedial measures required;5. Increase monitoring frequency to check mitigation effectiveness. <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none">1. Review the investigation results submitted by the ET;2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;3. Advise the ER on the effectiveness of the proposed remedial measures. <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none">1. Confirm receipt of notification of failure in writing;2. Notify Contractor;3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;4. Supervise the implementation of remedial measures. <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none">1. Submit noise mitigation proposals to IEC and ER;2. Implement noise mitigation proposals. <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit Level being exceeded	<ol style="list-style-type: none">1. Inform IEC, ER, Contractor and EPD;2. Repeat measurements to confirm findings;3. Increase monitoring frequency;4. Identify source and investigate the cause of exceedance;5. Carry out analysis of Contractor's working procedures;6. Discuss with the IEC, Contractor and ER on remedial measures required;7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;8. If exceedance stops, cease additional monitoring. <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none">1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none">1. Confirm receipt of notification of failure in writing;2. Notify Contractor;3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;4. Supervise the implementation of remedial measures;5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none">1. Take immediate action to avoid further exceedance;2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification;3. Implement the agreed proposals;4. Submit further proposal if problem still not under control;5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated. <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>

**Event / Action Plan for Construction Air Quality**

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; 2. Repeat measurement to confirm finding; 3. Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	1. Identify source; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
LIMIT LEVEL				
1. Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD; 2. Repeat measurement to confirm finding; 3. Increase monitoring frequency to daily; 4. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)



Event and Action Plan for Marine Water Quality

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Limit level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC, contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures; As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities. (The above actions should be taken within 1 working day after the exceedance is identified)



Appendix 6.1

Complaints Log



Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
100321a	21/3/2010	ICC Case no. 1-224618029, Ms. Tsang	Location near Tin Hau	Complaint regarding the loud noise and dark smoke in the course of dredging works on 21 March 2010 (Sunday).	<ol style="list-style-type: none">1) A valid Construction Noise Permit no. GW-RS0119-10 was granted from EPD since 18th Feb. 2010 for the dredging works which carry out at area for North Point Reclamation.2) Officer from Marine Department, Police and EPD's officer attended the scene for inspection and investigation.3) The Contractor (CHEC-CRBC JV) strictly comply all the conditions in CNP and take all mitigation measures in order to minimize the potential impacts to surrounding sensitive receivers. A formal letter was issued out by CHEC-CRBC JV and to explain the status of the recent construction activities.4) No limit level exceedance was recorded on the noise measurement during day time and evening time noise measurement on 23 March 2010. Additional restrict hours noise monitoring at Causeway Bay Community and City Garden was conducted on 5 April 2010 (Public Holiday). No limit level exceedance was recorded in the monitoring.5) No further complaints were received from Mr. Tsang in the reporting month. The complaint is considered closed.	Closed
100321b	21/3/2010	Unknown	Near the eastern breakwater of the Causeway Bay Typhoon Shelter	A public complaint and enquiry regarding loud noises emanated from dredging activities on 21/3/2010 (Sunday) until 2220 hours and between 1920-1946 hours in the evening of 22 March 2010(Monday).	<ol style="list-style-type: none">1) A valid Construction Noise Permit no. GW-RS0119-10 was granted from EPD since 18th Feb. 2010 for the dredging works at area for North Point Reclamation during general holidays including Sunday between 0700-2300 hours and any day not being a general holiday between 1900-2300hours. It is complied with the condition of CNP.2) Officer from Marine Department, Police and EPD's officer attended the scene for inspection and investigation.3) No limit level exceedance was recorded on the noise measurement during day time and evening time noise measurement on 23 March 2010. Additional restrict hours noise monitoring at Causeway Bay Community and City Garden was conducted on 5 April 2010 (Public Holiday). No limit level exceedance was recorded in the monitoring.4) No further complaints were received in the reporting month. The complaint is considered closed.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
100504	4/5/2010	Public complainant received by ICC (ICC case: 1-233384048)	Watson Road	Complaint on the noise nuisance due to the large scale of dredging machine (face to Island East Corridor) in particular the hours 1900 to 0800 and request to reduce the noise level.	1) Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0119-10 for their dredging works. Contractor has implemented mitigation measures to reduce the working hour not later than 2230. 2) According to RSS 's record, no more daytime and night time dredging since the departure of the split hopper barge from the workplace on 29 April 2010 at 1900 hrs to 5 May 2010. 3) No further complaints were received in the reporting month. The complaint is considered closed.	Closed
100731	31/7/2010	Mr. Lee received by ICC (CC Case: 1-250702681)	Oil Street to Watson Road	Complaint on the noise nuisance due to the dredging works. Three construction plants were operated concurrently.	1) Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0371-10 for their dredging works. 2) There was only 1 grab dredger operated by Contractor within NPR project site area for dredging works. 3) No noise exceedance was recorded at noise monitoring station at Victoria Centre on 27 July and 3 August 2010 during daytime and evening time period. 4) It is considered as invalid from the EP and CNP point of view.	Closed
100812	12/8/2010	Mr. Wong, Harbour Heights (Management) Ltd.	Harbour Heights	Management office received their resident complained on the noise nuisance from the dredging works at the marine works area adjacent to the Harbour Height during the period from 0700 to 2200.	1) Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0371-10 for their dredging works. Contractor has implemented mitigation measures to reduce the working hour not later than 2230. 2) No noise exceedance was recorded at noise monitoring station at Victoria Centre on 10 and 17 August 2010 during daytime and evening time period. 3) It is considered as invalid complaint. No further complaints were received in the reporting month. The complaint is considered closed.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
101108	8/11/2010	Mr. Nip received by ICC (CC Case)	Sai Wan Ho	Visual concern around the seaside silt screen outside the WSD freshwater intake pump at Sai Wan Ho (Monitoring station ref no.. WSD15)	<ol style="list-style-type: none"> 1) Contractor for HY/2009/11 has been regular checked of condition and removal of trapped rubbish before the dismantling of the floating silt screen to be replaced by wall mount silt screen. 2) Follow-up action had been immediately carried out to check and clear the floating refuse around the seaside silt screen after receipt of the complaint. 3) Removal of seaside silt screen outside the WSD freshwater intake (WSD15) by contractor HY/2009/11 was checked and confirmed dated 9 November 2010. Silt screen has been deployed into the existing steel frame at WSD15 for the protection of WSD salt water intake. 	Closed
101110	10/11/2010	Mr. Wong, Harbour Heights (Management) Ltd.	Harbour Heights	Management office received their resident complained on the noise nuisance from the power mechanical equipment during the 0700 to 2200hrs	<ol style="list-style-type: none"> 1) Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0870-10 for their dredging works during evening time. Contractor has implemented mitigation measures to reduce the working hour not later than 2230. 2) No noise exceedance was recorded at noise monitoring station at Victoria Centre on 4 and 10 November 2010 during daytime and evening time period. 3) It is considered as invalid complaint. No further complaints were received in the reporting month. The complaint is considered closed. 	Closed
101203	3/12/2010, 01:45a.m.	The resident of Block 11, City Garden by ICC referral from Marine Department	North Point	Bad odour was generated from the dredging plant off North Point	<ol style="list-style-type: none"> 1) The first investigation was carried out by Marine Department patrol in the morning on 3 Dec 2010 at around 10:00 and revealed that a few working barges were anchoring in the vicinity without carrying out dredging work. 2) A further specific investigation inspection on contractor's backhoe barge in the vicinity of City Garden was jointly conducted with Engineer Representatives (AECOM/RSS), and ET on 8 Dec 2010 at 11:30. No bad odour was noted during the investigation. 3) Routine dredging operation of the backhoe barge was performed during the jointed investigation inspection and it was revealed that no bad odour was attributed by the dredged materials inspected. 	Closed
101206	6/12/2010	Ms Lui, the resident of 27/F, Block 10, City	City Garden, North Point	Two barges were generating noise at 22:00 on 6 December 2010 in which the noise from	<ol style="list-style-type: none"> 1) ET confirmed the following information with resident site staff on the complaint: <ul style="list-style-type: none"> • It was referred to the filling operation at North Point 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		Garden by ICC (ICC case: 1-266039336)		<p>filling operation was louder than the traffic noise & visual impact was generated due to the spot-light pointing directly to the complainant flat, suspected the filling operation was part of Wanchai Development Phase II;</p> <p>Complainant also raised the same complaint to District Councillor, Mr. Hui on 7 Dec 2010 regarding the night-time noise and suspected earlier start of work at 06:30. Complaint also requested for limiting the plant operating hours from 09:00-21:00.</p>	<p>Reclamation of Central Wan Chai Bypass site area instead of part of Wanchai Development Phase II;</p> <ul style="list-style-type: none">Two derrick barges were in operation at the time of complaint for placing 400 rockfill onto the excavation trench and for levelling the formation level to receive the pre-cast caisson seawall;Flood light on the control mast of derrick barge have no lighting shields for the prevention of glare of flood lights;No starting work on 7 Dec 2010 at 0630hours. <p>2) PME used in restricted hours were checked and confirmed compliant with valid CNP no. GW-RS0870-10. The noise level recorded on 6 Dec 2010 was complied with the noise criteria during restricted hour;</p> <p>3) It was found that the occasional noise nuisance might be caused by the hitting or scratching onto the rock surface during loading down the grab onto the Grade 400 rockfill;</p> <p>4) The absence of the lighting shields at flood light results in visual glare to the complainant at night-time.</p> <p>5) Contractor was advised to minimize the finishing time of placing Grade 400 rockfill at 2100hrs and switch off all unnecessary flood lights apart from the light for the safety and security purpose;</p> <p>6) No further complaint was received after implementation of proposed measures</p>	
110415	15/04/2011	The resident, Mr Law at Victoria Centre by ICC (ICC#1-281451236)	North Point	A dust generation and a concern of mosquitoes breeding complaint in which suspected the filling operation was part of North Point Reclamation.	<p>1) The concerned stockpile was a working stockpile under Contract HY/209/15 and was covered at night time after work.</p> <p>2) Water spraying on the haul road and potential dust generating material at least 4 times a day was conducted by contractor that complies with the requirement.</p> <p>3) It is considered invalid but preventive actions can be taken because the stockpile is relatively large and easily visible by complainant.</p> <p>4) It was recommended that increasing the frequency of water spraying shall be conducted to all potential dust generating materials and activities. Besides, Contractor should consider to cover the idle part of the stockpile</p> <p>5) The concern of mosquitoes breeding is out the scope of EM&A, the follow-up action is not reported in this monthly EM&A report.</p>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
110419	19/04/2011	Ms Chiu at Victoria Centre at Victoria Centre by ICC (ICC# 1-272874759)	North Point	The episode of night noise on 19/4/11 and 20/4/11 at 2:50 am and the noise lasted for 30 minutes per night.	<ol style="list-style-type: none">1) According to the RSS's record, there was no construction works undertaken under the EP-356/2009 during the concern time period.2) There was no abnormal real-time noise monitoring data recorded in RTN1 - FEHD Hong Kong Transport Section Whitefield Depot which is next to the Victoria Centre.3) It is considered as invalid complaint under this Project.	Closed
110617	9/06/2011	Mr. Law from Victoria Centre Management Office	North Point	An odour nuisance suspected generating from the discharge point – Channel T at Watson Road in part of the site area was related to CWB under Contract no. HY/2009/11	<ol style="list-style-type: none">1) The complaint was received by ET on 13 Jun 2011. During the weekly site inspection on 7 and 17 June 2011, there was no any odour impact detected in the site area.2) According to the site record, there was muddy water discharged from the unknown source at upstream of Channel T during heavy rainstorm. No any site surface runoff to the Channel T and out of site boundary was observed in the inspection.3) In order to prevent muddy water washing out to the water body under heavy rainstorm, a silt curtain was installed at the outfall of the channel by Contractor. ET confirmed with the Resident Site Staff that a silt curtain was installed at the outfall of the channel to prevent muddy water washing out to the water body under heavy rainstorm. Besides, regular cleaning of refuse in the channel has been conducted by Contractor.4) A further site investigation on 28 June 2011 revealed that no odour nuisance was detected at the upstream of the Channel T and no source of odour nuisance was identified at site. As such, it was concluded that the source of odour nuisance was not related to the Project works.5) Although no source of odour nuisance was identified at site, the muddy water and dirt from the unknown source at upstream of Channel T may cause a potential smell during low tide and low water flow. Contractor was reminded to remove the silt curtain at the channel on non-rainy day so as to avoid the accumulation of the sediment and dirt in the water channel.	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
110709	09/07/2011	Mr. Au from City Garden Management Office	North Point	A complaint letter to Contractor HY/2009/11 was raised by Cayley Property Management Limit on 9 July 2011 regarding a series of pump breakdown events at seawater intake of City Garden on 4, 6, 7 and 8 July 2011. A lot of rubbish such as plastic bags, nylon bags, nylon-wire mesh was observed sucking from the seawater intake at the seawater front of Block 7 of City Garden affecting the operation of seawater pump plant.	<ol style="list-style-type: none"> Contractor conducted formation works for installation of caisson seawall at C27, C28, C29 and C30 on 4, 6, 7 and 8 July 2011 and no dredging work was conducted during this time period Water mitigation measures of an 80m long silt curtain at the site boundary in front of City Garden Relocation of silt curtain and silt curtain at the outfall of the channel were provided and maintained to accommodate the site works. All vessels are equipped with rubbish collection facilities and disposed the rubbish regularly. Also, daily cleaning actions had been taken by contractor to minimize floating refuse within the site boundary. Moreover, it has been reported several times that discharged from outfall pipeline outside the site boundary near the intake of the pump maybe considered as another source of rubbish generation. Referring to the record provided by Cayley Property Management Limit, the trapped rubbish was unlikely generated from the construction works. It was considered that complaint is invalid and not related to project. 	Closed
110710	09/07/2011	Complainant by ICC (ICC no. 1-301520309)	North Point	It was received at 00:56 on 10 July 2011. There was complained a derrick barge unloading rockfill material off the shore facing the Harbour Grant HK Hotel causing noise nuisance.	<ol style="list-style-type: none"> ET confirmed with the Resident Site Staff that the complaint was referred to Contract HY/2009/15 for the loading and unloading of fill material at two barges operation in the sea at around 300m adjacent to Island Eastern Corridor (Oil Street Chainage) where is outside the Site of HY/2009/15 in the period of around 19:45 on 9 July to 1:00 on 10 July 2011. The material loading and unloading operation processed in restricted hours was checked without a valid CNP. It was found that the operation was due to an unexpected water leakage of the hopper barge and considered an incident. According to the incident report provided from RSS on 20 July 2011, around 7:30 pm the barge S22 was inclined slightly and slightly water leakage might occur. Due to marine safety concern, the hopper barge would open the hopper to release the contained materials in order to reduce the weight and stabilize the barge. In consider of slight water leakage, the operator decided to use the nearby Derrick Barge ST32 to help for unload the general fill materials first and the unloading operation was started at around 7:45pm, and end at around 1:00 am. Contractor was reminder to provide frequent check of vessel condition 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					so as to prevent recurrent by barge defect	
110723a	23/07/2011	Ms. Law at Victoria Centre by ICC no. 1-303887687	North Point	She concerned that Highways Department published a notice in their Management Office about construction works will be conducted from 0700 hours to 2300 hours during July to December 2011 including Saturday, Sunday and public holiday.	<ol style="list-style-type: none"> 1) It was referred by AECOM to ET on 28 July 2011 2) RSS confirmed that the notice was prepared by Victoria Centre's Management office to their resident and the advice was only given on the extension construction works (for Contract HY/2009/15) to 7am-9pm from Monday to Saturday except Public Holidays and Sundays. 3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid-August 2011. 4) No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring. 5) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures. 	Closed
110723b	23/07/2011	Ms. Yau at Block 2, Victoria Centre by ICC no. 1-304013959	North Point	Reclamation work was conducted at Causeway Bay Typhoon Shelter at 7am on 23 July 2011. She complained that the works shall be started later to minimize the noise nuisance to the vicinity of the residents in early morning	<ol style="list-style-type: none"> 1) It was referred by AECOM to ET on 8 August 2011 2) With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring 3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid-August 2011. 4) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures. 	Closed
110727a	27/07/2011	Mr. Law from Victoria Centre Management Office by ICC no. 1-304616162	North Point	It was complained by Mr. Law from Victoria Centre Management Office on 27 July 2011 regarding construction noise generated by the construction operations of	<ol style="list-style-type: none"> 1) It was referred by AECOM to ET on 28 July 2011 2) RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents. 3) No noise exceedance was recorded at construction noise 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Central-Wanchai Bypass at noon rather than in morning at 7am.	<p>monitoring station at Victoria Centre on 25 July and 4 August 2011 during daytime while breaking and excavation works were undertaken during monitoring.</p> <p>4) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. No further complaint from complainant was received after proposed the mitigation measure.</p>	
110727b	27/07/2011	Ms. Chiu by ICC no.1-304615409	North Point	Noise nuisance from the excavation works for the Highways Department adjacent to the Victoria Centre was conducted from 7am	<p>1) It was referred by AECOM to ET on 28 July 2011</p> <p>2) With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 25 July and 4 and 10 August 2011 during daytime while breaking and excavation works were undertaken during monitoring.</p> <p>3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am.</p>	Closed
	08/08/2011				<p>4) However, complainant did not satisfy with the response on the noise nuisance from the rock-breaking during morning in front of Victoria Centre and then further complaint via 1823 on 7 August 2011.</p> <p>5) Highways contacted the complainant on 15 August 2011 that the noisy rock breaking operation had been completed.</p> <p><i>Remarks: There will be counted as two complaints in this complaint log.</i></p>	
110810	10/08/2011	Mr. Yip by ICC no. 1 - 306740207	North Point	Muddy water was discharged from work site to the seafront near Oil Street during heavy rain. The environmental protection measures were not good enough and are needed to rectify.	<p>1) It was referred by AECOM to ET on 17 August 2011.</p> <p>2) Confirmed with RE, Muddy water was caused by a heap of earth being washed to the sea by heavy rain. The heap of earth was referred as a small stockpile placed close to the seafront in front of Oil Street within the site area under handover transition period from contract HY/2009/11 to contract HY/2009/19. The necessary mitigation measures to protect the small stockpile against rainfall were missing at the time of complaint.</p> <p>3) Due to the missing of mitigation measures to protect the small stockpile during handover transition period, loose material was washed into the harbour when heavy rain came. Muddy water was formed and dispersed in the sea that caused the water quality and visual concern to the public. The complaint was considered as valid.</p> <p>4) Contractors were advised to relocate the loose materials</p>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					away from the coastline as far as practicable. Any loose material placed which needed to be placed near the coastline shall be properly compacted or covered as appropriate. To avoid any further environmental deficiency, Contractors shall ensure all necessary environmental mitigation measures will not be missing during site area handover.	
110826	26/08/2011	Grand Hyatt and a complainant by ICC	Wan Chai	Construction noise and vibration nuisance generated from the works at Convention Avenue and inside the HKCEC1 reclamation area.	<ol style="list-style-type: none">1) Confirmed with the Resident Site Staff that the construction works were referred to the Contractor HK/2009/01.2) The Excavator mounted breaker at Convention Avenue and Drilling rig at HKCEC1 reclamation area were the dominant construction noise source during this period.3) The drilling rig at HKCEC1 reclamation area and excavator mounted breaker at Convention Avenue were then temporary suspended after received the complaint.4) Investigation revealed that the erected noise barrier (4m cantilevered movable noise barrier for the drilling rig and 1m movable noise barrier for the excavator mounted breaker) were not located close to the plants to provide adequate noise screening.5) Contractor was advised to avoid concurrent operation of construction plants at site. Further enhancement of movable noise barriers at HKCEC1 and providing noise enclosure for the excavator mounted breaker at Convention Avenue are needed.6) Further site investigation and checking on 31 August and 7 September 2011 revealed that the implemented noise mitigation measures were in proper and minimize the noise impact.	Closed
110826A	26/08/2011	A complaint letter from Mr. Au of Cayley Property of City Garden	North Point	Harbor front adjacent to their cooling water intake suction which caused 3 times of system breakdown of the sea water pump on 9, 22 and 25 August 2011.	<ol style="list-style-type: none">1) It was referred by AECOM to ET on 29 August 2011. Confirmed with the Resident Site Staff that the<ul style="list-style-type: none">• construction works were referred to the Contractors HY/2009/11 and HY/2009/19.• The pump is located on the site area of HY/2009/19• A temporary garbage defender was installed on 23 July 2011 by HY/2009/11 and the shape of the defender was adjusted on 8 August 2011 in order to exclude the outfall.• An ad hoc inspection of the effectiveness of garbage defender was conducted with RSS (CWB project	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>team), contractor of HY/200911 and HY/2009/19 and IECon 29 August 2011. Inspection report of it was submitted to RSS on 19 September 2011.</p> <ul style="list-style-type: none">• Daily cleaning near the water intake was conducted twice a day by contractor HY/2009/19.• In response to City Garden request, the contractors have set up the temporary garbage defender in function and collect the floating refuses, but cannot eliminate all refuses, in particular the refuse coming from the seabed <p>2) According to the complaint letter from Cayley Property, the outcomes of the preventive measures were not complying with their expectation.</p> <p>3) During on-site inspection, floating refuses observed occasionally outside the garbage defender. No conclusion could be made for the source of these floating refuses. On the other hand, some of the refuses were observed floating behind the garbage defender during investigation.</p> <p>4) All daily cleaning actions had been taken by contractor to minimize floating refuse inside the construction site.</p> <p>5) It was noted that the cooling water intake was accessible to the public. As such, fish breeding and fishing activities were observed even though a notice has already hoisted. Also, tripping of rubbish by the passers-by could result in a lot of rubbish accumulated around the intake point.</p> <p>6) Referring to the record provided by CPML, there were a lot of nylon/ plastic bags and nylon wire mesh that matched those rubbishes generated from the public activities.</p> <p>7) Contractors have fulfilled the requirement of site cleanliness and no exceedance was recorded during Water Quality Monitoring. It is considered the cause of this complaint is not related to project and environmental issue in this project as well. No more complaint received after ad-hoc inspection</p>	
111014	14/10/2011	The complainant, Ms. Tam complained via hotline 1823	Wan Chai	The polluted fumes and exhaust from the excavation by sub-contractor of CEDD on pedestrian way outside no.25 Harbour Road (in front of the Harbour Centre)	<p>1) RSS notified ET to carry out investigation on 17 October 2011.</p> <p>2) ET confirmed with the Resident Site Staff that the location of the excavator was within site area of Contract no. HK/2009/02 undertaking the water cooling main re-provision works along the Harbour Road. The plants including the excavator have been checked before using</p>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					at the site. However, the polluted fumes and exhausted from the excavator was caused due to insufficient maintenance of the plant after using at site. 3) After receiving the complaint, the excavator was then removal off-site for checking and maintenance works on 17 October 2011. 4) Contractor was reminded to enhance regular checking and maintenance to all plants at site. 5) RSS has replied to the complainant on the arrangement of the measures taken on 17 October 2011. Complainant was satisfied with the response and follow-up action taken by the Contractor.	
111104	04/11/2011	Mr. Liu from LCSD complained via Contractor Complaint Hotline	Wan Chai	Complain about a tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road, the status is not healthy and roof ball of two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue were half cut.	1) ET confirmed with the Resident Site Staff that • A tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road is the Tree no. TA1122 under Contract no. HK/2009/02. Leaves of a branch of this tree were shrivelled. • Two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue are the tree nos. A160 and A161 under Contract no. HK/2009/01. Part of roof ball of these two trees was covered by the metal plate. 2) Independent Tree Specialists for these two inspected the trees. Contractor HK/2009/01 has taken the measure as recommend downgrading the soil level around the trunk base. Reinstating of the ground works will be conducted in mid-December 2011. For the tree no. TA1122 under Contract no. HK/2009/02, the brown leaves were removed and fenced the tree with orange net is provided to prevent damage of tree trunk by construction works. The distance between the tree and the edge of the trench is kept approximate 2m. Two Contractors were reminded to carry out regular watering to the trees within their site area.	Waiting RSS respond
111106	06/11/2011	Police officer	Wan Chai	Construction noise generated from the site at about 6:30 a.m on 6 November 2011 and require to stop the machine operation	1) According to the information reported by Contractor, one BC cutter and hoist were operated for Diaphragm Wall construction of Shatin-Central Link to inspect bentonite pipes and ensure no damages and all the joints are tightened in good position. Then, the subcontractor for Diaphragm wall, SAMBO Korean foreman stopped the engine of the BC cutter immediately. The police officer recorded the details and HKID number of the foreman and then left. Due to the different language communication between the police officer and the Korean foreman, no	Keep in view for three months from the date of complaint received



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>CNP was checked by the police officer.</p> <p>2) ET confirmed with the Resident Site Staff that same issue was also raised out by RSS at about 7:00a.m on the same day. Besides, it was confirmed that there is no valid Construction Noise Permit for the conducted construction works in the period between 2300 and 0700.</p> <p>3) Due to insufficient communication between Contractor HK/2009/01 and their Korean Sub-contractor, Korean Sub-contractor had not notified to Contractor before carrying out the inspection of the BC cutter, hoists and bentonite pipes at about 6:00a.m to ensure no damages and all the pipe joints should be tightened and in good position.</p> <p>4) Contractor was advised to enhance the communication between Contractor and sub-contractor and provide sufficient environmental training to all foreman and operators on restricted hour operation. Furthermore, Construction Noise Permit should be checked and in place for the construction works during restricted hour</p> <p>5) This complaint was considered in relation to the conducted construction works during restricted hours without valid Construction Noise Permit. No more construction works were conducted during night time period. The construction works will be conducted in accordance with the time period stated in valid CNP. This complaint will be kept in view of any follow-up action from the relevant government activities.</p>	
120405	05/04/2012	N/A	North Point	A complaint regarding excessive noise from construction sites of CBTS was observed daily before 7:30am except on public holidays, and the noise source was mainly from piling works. The complainant requested that construction works should start after 8:30am to avoid nuisance to nearby residents and a speedy follow-up and reply.	<p>1) RSS notified ET on 5 April 2012.</p> <p>2) ET confirmed with the Resident Site Staff that no piling works were performed during the concerned period.</p> <p>3) After reviewing the results of noise monitoring (M2b and M3a), no exceedance was recorded during daytime period and the noise level was below 75dB(A). Site inspection for HY/2009/15 was conducted on 10 April 2012. The condition of noise mitigation measures around CBTS was found satisfactory. RSS confirmed that no pilings were performed during the concerned period. The major works included drilling, diaphragm wall construction and excavations.</p> <p>4) HyD made a reply to the complainant on 16 April 2012 via 1823. HyD replied that the current works at CBTS were drilling, diaphragm wall construction and deep excavations. In order to minimize the noise generated</p>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					from the above works, the Contractor had erected temporary noise barriers and provided noise blankets on plants. RSS would continue to work with the Contractor on the effectiveness of the environmental mitigation measures implemented on site. No further complaint was received after the response.	
130308	06/03/2013	ICC Case#1-407181502	Tin Hau	A complaint regarding the dropping of fine rock material into surrounding waterbody was observed during rock breaking operation with two excavators in active operation at the Eastern Breakwater of Causeway Bay Typhoon Shelter near the North Point lighthouse.	<p>1) RSS notified ET on 8 March 2013</p> <p>2) ET confirmed with RSS that excavation works, installation of buoy, flashing light and silt curtain and dredging works were undertaken at Eastern Breakwater during the concerned period on 6 March 2013. One backhoe equipped with breaker and one derrick barge were confirmed in operation while another backhoe was at idle during the concerned period on 6 March 2013.</p> <p>3) Reviewing the photo record provided by RSS, the condition of the silt curtain deployed around the Eastern Breakwater on 6 March 2013 was found to be in good condition. It is considered that the silt curtain was properly in place during the concerned period and the concerned act of dropping of fine rock material was confined within the silt curtain boundary without adverse impact to the nearby water quality.</p> <p>Further follow up was conducted on 12 March 2013 during weekly environmental audit inspection, the silt curtain deployed around the concerned area was found to be maintained in good condition and the water quality at the concerned work area was generally satisfactory. No violation of the Environmental Permit condition was found.</p> <p>The contractor was advised and committed to implement preventive measures to minimize the potential impact of work including conducting regular diver check to ensure the integrity and the extend of silt curtain deployment and to provide adequate back up stock of silt curtain for emergency use.</p>	Closed
140612	12/06/2014	EPD ref: EP/860/F2/24 Annex IV	Wan Chai	The complaint is regarding to the water quality of the waterfront outside the Hong Kong Academy for Performing Arts Theatre Block, where a large piece of muddy water was found.	<p>1) WSII RSS team notified ET on 12 June 2014; Notification letter from EPD (ref: EP/860/F2/24 Annex IV) was received by ET on 13 June 2014.</p> <p>2) ET confirmed with RSS that neither marine construction works nor barge operation was conducted at the concerned location during the time of complaint. With respect to the complaint case, muddy dispersion was observed at HKCEC2W works area on 12 June 2014, and</p>	Interim Report was submitted to EPD on 20 June 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>the dispersion was observed partly extended beyond the outermost layer silt curtain at 1000hrs. Immediate follow up action was requested.</p> <p>3) It is considered that Contractor's mitigation measures would require further review on the effectiveness to avoid seepage of muddy dispersion such as regular diver inspection check and daily visual checking of silt curtains.</p> <p>Additional silt curtain at marine access zone was installed by Contractor on 12 June 2014 and the double layer silt curtain were generally in order. Follow-up inspection was further conducted on 16 June 2014.</p> <p>The Contractor's investigation report on the complaint case was submitted to EPA via email on 18 June 2014.</p>	
140723	21/07/2014	ICC Case Ref: 2-341537112	Works area opposite to Ngan Tao Building	The complaint is regarding to construction noise impact to the complainant who could not sleep due to work and machine at the project site opposite to the Ngan Tao Building.	<p>1) Construction noise impact referred by RSS was received by ET on 25 July 2014</p> <p>2) ET confirmed with RSS that horizontal cutting and removal of D-wall at Eastern, Southern and Northern side of TS2 was undertaken by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter before 23:00hrs on 20 July 2014 that total 3 numbers of derrick lighter and 3 numbers of saw cut machine were in operation, and removal of D-wall at Panel S30A-1 of TS2 was undertaken by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter around 00:25hrs to 00:56hrs on 21 July 2014 that total 1 number of derrick lighter was in operation.</p> <p>3) According to the relevant site records under Contract HY/2009/15, before 23:00hrs on 20 July 2014, horizontal cutting and removal of Diaphragm Wall at Eastern, Southern and Northern side of TS2 was conducted under HY/2009/15 within Causeway Bay Typhoon Shelter. Total 3 nos. of derrick lighter and 3 nos. of saw cut machine were in operation at the above period. From around 00:25hrs to 00:56hrs on 21 July 2014, removal of D-wall at Panel S30A-1 of TS2 was undertaken by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter. Total 1 no. of derrick lighter was found operating at the above period</p> <p>4) It was considered the condition of CNP GW-RS0592-14 was not fulfilled by the Contractor of HY/2009/15. "From 00:25hrs to 00:57hrs on 21 July 2014, the PME(s) (1 no. of Derrick Lighter) on-site could not follow with any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in no. GW-RS0592-14."</p>	<p>Final report (Issue1) issued on 31 July 2014.</p> <p>Further to complainant follow-up, Final report (Issue2) Issued on 12 Aug 2014.</p>



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>Notwithstanding the above, according to the site recorded provided by the RSS, the derrick lighter was found malfunction at around 23:00hrs on 20 July 2014 while the diaphragm wall cutting procedure was incomplete. Under safety and navigation consideration, the completion of diaphragm wall removal was necessary and of imminent need.</p> <p>5) The Contractor of HY/2009/15 was advised to review the construction sequence and emergency response procedure for construction activities during restricted hours and night time period to allow for sufficient buffer time for work completion such that the Construction Noise Permit would be followed. Furthermore, the Contractor of HY/2009/15 was suggested to conduct throughout checking of PME used on site prior to work commencement to minimize the potential malfunctioning of PME during the course of work which affect the duration of works.</p>	
141016	14/10/2014	EPD Ref.: EP860/E2/24 Annex IV ICC complaint received by ET on 10 October 2014	Work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	Construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	<p>A public complaint regarding construction noise impact referred by EPD was received by ET on 16 October 2014 (EPD Ref.: EP860/E2/24 Annex IV dated 16 October 2014). The complainant reported that construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.</p> <p>ET confirmed with the Resident Site Staff that From 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</p> <p>From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</p>	<p>Interim investigation report submitted to EPD on 23 October 2014.</p> <p>Updated interim investigation with supplementary information submitted to EPD on 17 November 2014</p>



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway.</p> <p>Total one scissor platform and two hand held drills (battery) were in operation.</p> <p>From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road.Total one crane lorry was in operation.</p> <p>According to the relevant site records under Contract HK/2009/02, from 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</p> <p>From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</p> <p>From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway. Total one scissor platform and two hand held drills (battery) were in operation.</p> <p>From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road. Total one crane lorry was in operation.</p> <p>In view of the above findings, no direct information associated with the noise concern was considered available.</p>	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
141110	07/11/2014	EPD Ref.: H05/RS/000278 15-14 EPD complaint received by ET on 10 November 2014	Construction site at old Wan Chai Ferry Pier	Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool.	<p>A public complaint regarding odour concern referred by EPD was received by ET on 07 November 2014 (EPD Ref.: H05/RS/00027815-14 dated 10 November 2014).</p> <p>The complainant reported that Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool.</p> <p>ET confirmed with the Resident Site Staff that</p> <p>ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool).</p> <p>Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated.</p> <p>Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier.</p> <p>Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.</p> <p>Dredging works was conducted on 7 November 2014 during daytime at WCR3 (East of old Wan Chai Ferry Pier)</p> <p>Total 1 no .of dredger, 1 no. of hopper and 1 no. of tug boat were operated.</p> <p>According to the relevant site records under Contract HK/2009/02, ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool). Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated. Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.</p> <p>Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site. The condition of chemical waste storage was considered satisfactory and no malodour was identified. Despite no information related to malodour was identified, the Contractor was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.</p>	<p>Interim investigation report submitted to EPD on 17 November 2014.</p> <p>EPD advised no comment on the interim report and case closed on 1 Dec 2014.</p>



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Based on the relevant information provided by RSS, despite no information associated with the malodour concern was identified after investigation, the Contractor was reminded to conduct regular checking on the condition of PME used on site to ensure only well maintained PME are used on site The interim report would be submitted to EPD on 17 November 2014.	
141113	12/11/2014	EPD Ref.: H05/RS/000282 53-14 EPD complaint received by ET on 13 November 2014	Construction site at old Wan Chai Ferry Pier	Malodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians.	<p>A public complaint regarding odour concern referred by EPD was received by ET on 13 November 2014 (EPD Ref.: H05/RS/00028253-14 dated 13 November 2014). The complainant reported that Malodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians. (Contract HK/2009/02)</p> <p>ET confirmed with the Resident Site Staff that demolition works was conducted under Contract HK/2009/02 on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated.</p> <p>According to the relevant site records under Contract HK/2009/02, demolition works was conducted on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated.</p> <p>In addition, investigation found that due to malfunctioning of one of the excavators deployed at old Wan Chai Ferry Pier, dark smoke was emitted from the defective excavator for a short period of approximately 30 seconds at around 15:00 hrs on 12 November 2014. The operation of excavator was immediately suspended and followed by repair works. The normal operation of the excavator was resumed after repair.</p> <p>Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site and the Contractor of HK/2009/02 was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.</p>	<p>Interim investigation report submitted to EPD on 19 November 2014.</p> <p>EPD advised no comment on the interim report and case closed on 8 Dec 2014.</p>



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
141121	Not Specified	EPD Ref: H08/RS/28263-14 EPD complaint information and findings was received by ET via email on 21 Nov 2014	Causeway Bay Typhoon Shelter	Resident in Hing Fat Street complaining about loud noise from dredging work in CBTS up to 10pm at night.	EPD received a construction noise complaint from dredging works at Causeway Bay Typhoon Shelter and a resident in Hing Fat Street complaining about loud noise from dredging work in CBTS up to 10pm at night. EPD investigation found that the operation of a derrick barge is covered by CNP no. GW-RS0701-14. EPD reminded the Contractor of HY/2011/08 to ensure the work strictly follow the permit conditions and endeavor to minimize the noise as so not to disturb the nearby residents.	Complaint case handled by EPD and relevant investigation findings was sent to ET on 21 November 2014
150127	21 Jan 2015	EPD complaint (EPD Ref.: H05/RS/00001725-15) received by ET on 27 January 2015 and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015	A portion of Hung Hing Road immediately to the east of Marsh Road near SPCA	Construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public.	A public complaint regarding air quality impact referred by EPD was received by ET on 27 January 2015 (EPD Case Ref.: H05/RS/00001725-15 dated 27 January 2015) and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015. The complainant reported that construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public. ET confirmed with the Resident Site Staff that the major construction activities around the concerned location conducted on 21 January 2015 include breaking of seawall blocks and D-wall at TPCWAW; concreting, grouting and drilling works at TPCWAW;reclamation/ backfilling works at TPCWAW Mitigation measures implemented by the Contractor for the above construction works include spraying haul road with water; covering bagged cement with tarpaulin; providing three sided and top covering for grouting stations; providing water spraying to dusty activities such as breaking works According to the relevant site records, breaking of seawall blocks and D-wall, concreting, grouting and drilling works and reclamation/ backfilling works were	Interim report submitted to EPD on 9 February 2015



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>conducted at TPCWAW. Dust mitigation measures including spraying haul road with water, covering bagged cement with tarpaulin, providing three sided and top covering for grouting stations and water spraying to dusty activities such as breaking works were implemented by the Contractor of HY/2009/15 near the concerned location on 21 January 2015.</p> <p>Follow-up investigation was conducted on 27 January 2015 during weekly environmental inspection, dust mitigation measures including water spraying for dusty haul road and major dust generation works; and provision of three sides and top covering for grouting station were confirmed in place.</p> <p>In addition, based on the review of the monitoring data of the monitoring station located at the concerned location raised by the complainant, namely monitoring station CMA3a , no action or limit level exceedance was recorded during air quality monitoring conducted on 20 and 21 January 2015. Nevertheless, the Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on the complaint date was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants.</p> <p>As such, the site condition under Contract HY/2009/15 at the concerned location was considered to be generally satisfactory and no non-conformity related to cumulative air quality impact was observed. Nevertheless, in view of the public concern, the contractor was reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.</p>	



Appendix 7.1

Construction Programme of Individual Contracts

CEDD CONTRACT HK/2009/01

CHUN WO - LEADER JOINT VENTURE

Activity ID	Activity Name	OD	Start	Finish	Total Float	Predecessors
HK/2009/01 - Revised Works Programme Updated (Data Date: 20-Jan-15)						
Key Dates (Contractual)		48	20-Feb-15	02-Apr-15	589	
Major Works						
KD-0300	Completion of Section 3 of Works - CWB, Slip Roads 2 & 3 & Works in Area 8	0		11-Mar-15*	0	KD-0305, PRE-4050
KD-0400B	Completion of Outstanding Works for Section 4 - Salt Watermains	0		02-Apr-15	500	TTAM-B6-1030B, TTAM-A2-1040D, TTAM-A3-1090B, TTAM-A5-1050B, TTAM-B6-1090B
KD-0610	Completion of Section 6A of Works - Gov't Offices cooling water discharge	0		20-Feb-15*	-122	TTAM-C2-1100B, TTAM-X3-1000B, KD-0615, TTAM-C2-1100B
KD-0620	Completion of Section 6B of Works - Great Eagle Centre cooling water discharge	0		20-Feb-15*	-122	KD-0625, TTAM-C2-1100B, TTAM-X2-1020B, TTAM-C2-1100B
KD-0630	Completion of Section 6C of Works - China Resources Bldg cooling water discharge	0		20-Feb-15*	-122	TTAM-C2-1100B, TTAM-X2-1020B, KD-0635, TTAM-C2-1100B
KD-0800	Completion of Section 8 of Works - Works in Area 5	0		20-Feb-15*	-105	KD-0805
KD-1200	Completion of Section 12 of Works - Works in Area 10	0		20-Feb-15*	-316	KD-1205
KD-1300	Completion of Section 13 of Works - Works in Area 11	0		20-Feb-15*	-29	KD-1305
Landscaping & Establishment Works						
Key Dates (Forecast Completion)		135	20-Feb-15	18-Jun-15	501	
Major Works						
KD-0405B	Completion of Outstanding Works for Section 4 - Salt Watermains & Works in Area 3	0		20-Feb-15	542	S11-4030, S4-2520, S4-4060, S4-4000, S4-1500, S4-4070, S4-4050, S4-2500, S4-4090, S4-4010, S6-1030, S6A-2010, S6A-2030B
KD-0615	Completion of Section 6A of Works - Gov't Offices cooling water discharge	0		18-Jun-15	-241	S6B-2000, S6-1030, S6B-2020B
KD-0625	Completion of Section 6B of Works - Great Eagle Centre cooling water discharge	0		18-Jun-15	-241	S6C-2000, S6-1030, S6C-2020B
KD-0635	Completion of Section 6C of Works - China Resources Bldg cooling water discharge	0		18-Jun-15	-241	S6C-2000, S6-1030, S6C-2020B
KD-0805	Completion of Section 8 of Works - Works in Area 5	0		22-May-15	-196	S8-3000
KD-1205	Completion of Section 12 of Works - Works in Area 10	0		28-Feb-15*	0	TTAM-A4-1050C, S12-1000, TTAM-A4-1020B, VO105-1000, VO105-1000A
KD-1305	Completion of Section 13 of Works - Works in Area 11	0		28-Feb-15*	0	S3A-TS-1050, S13-1000, S13-3000, S13-2000, VO105-2000, VO105-2000A
Landscaping & Establishment Works						
Possession of Site Preliminaries		0			0	
Preliminaries		1510	04-Mar-11 A	21-Apr-15	481	
Method Statement & Design (Major Approval by MCDOT)						
PRE-2000G	D-Wall Construction for CWB Tunnel (Stage 3)	60	05-Nov-13 A	20-Feb-15*	-426	PRE-2000E

Remaining Work

Actual Work

Summary Bar

Critical Remaining Work

Milestone

CEDD CONTRACT NO. HK/2009/01

Wan Chai Development Phase II - Central-Wan Chai Bypass at HKCEC (Contract 1)

WORK PROGRAMME Rev. 6E 3mths Rolling Programme (Data Date on:20-Feb-15)

Page: 1 of 8

CHUN WO - LEADER JOINT VENTURE

[illegible]

CEDD CONTRACT HK/2009/01

CHUN WO - LEADER JOINT VENTURE

Activity ID	Activity Name	OD	Start	Finish	Total Float	Predecessors	2011				2012				2013				2014				2015																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
							Ctr 1	Ctr 2	Ctr 3	Ctr 4	Ctr 1	Ctr 2	Ctr 3	Ctr 4	Ctr 1	Ctr 2	Ctr 3	Ctr 4	Ctr 1	Ctr 2	Ctr 3	Ctr 4	Ctr 1	Ctr 2	Ctr 3	Ctr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
							M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J	F	M	A	M	J	J

CEDD CONTRACT HK/2009/01

CHUN WO - LEADER JOINT VENTURE

[illegible]

CEDD CONTRACT HK/2009/01








CHUN WO - LEADER JOINT VENTURE

[illegible]

CEDD CONTRACT HK/2009/01

CHUN WO - LEADER JOINT VENTURE

[illegible]

 Remaining Work  Summary
 Actual Work  Summary Bar
 Summary Bar
 Critical Remaining Work
 Milestone

CEDD CONTRACT NO. HK/2009/01

Wan Chai Development Phase II - Central-Wan Chai Bypass at HKCEC (Contract 1)

WORK PROGRAMME Rev. 6E 3mths Rolling Programme (Data Date on:20-Feb-15)

Page: 6 of 8

CEDD CONTRACT HK/2009/01








CHUN WO - LEADER JOINT VENTURE

[illegible]

CEDD CONTRACT HK/2009/01

CHUN WO - LEADER JOINT VENTURE

[illegible]

 Remaining Work  Summary
 Actual Work  Summary Bar
 Summary Bar
 Critical Remaining Work
 Milestone

CEDD CONTRACT NO. HK/2009/01

Wan Chai Development Phase II - Central-Wan Chai Bypass at HKCEC (Contract 1)

WORK PROGRAMME Rev. 6E 3mrths Rolling Programme (Data Date on:20-Feb-15)

Page: 8 of 8

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015																	
						March				April				May				June					
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21		
3MRP - March 2015 to June 2015																							
02 - PRE-CONSTRUCTION WORKS																							
02.3 - Method Statement / Shop Drawings																							
0230-1380	MS Landscape Deck Structure - Submission	28	20-Mar-15	16-Apr-15	854																		
0230-1390	MS Landscape Deck Structure - ER Review & Comment	28	17-Apr-15	14-May-15	854																		
0230-1400	MS Landscape Deck Structure - Resubmission	28	15-May-15	11-Jun-15	854																		
0230-1611	MS Noise Semi Enclosure - Submission	60	20-Mar-15	18-May-15	256																		
0230-1612	MS Noise Semi Enclosure - ER Review / Comment	28	19-May-15	15-Jun-15	256																		
0230-1690	MS Approach Ramp - ER Approval	14	01-Feb-15 A	02-Apr-15	289																		
A10110	MS for Partition Walls and outstanding columns at APS Basement - ER No Adverse Comment	9	01-Feb-15 A	28-Mar-15	7																		
A10520	MS EVB Basement & Mezzanine Construction - No Adverse Comment	14	04-Apr-15	17-Apr-15	26																		
A10640	MS for Demolition of existing Westbound Bridge - Submission	7	20-Feb-15 A	26-Mar-15	2																		
A10650	MS Demolition of existing Westbound Bridge - ER Review / Comment	14	27-Mar-15	09-Apr-15	2																		
A10660	MS Demolition of existing Westbound Bridge - Resubmission	14	10-Apr-15	23-Apr-15	2																		
A10670	MS Demolition of existing Westbound Bridge - No Adverse Comment	14	24-Apr-15	07-May-15	2																		
A10680	MS for Connection of EVB and EVA - Submission	10	10-Mar-15 A	29-Mar-15	1																		
A10690	MS for Connection of EVB and EVA - ER Review & Comment	12	30-Mar-15	10-Apr-15	1																		
A10700	MS for Connection of EVB and EVA - Resubmission	6	11-Apr-15	16-Apr-15	1																		
A10710	MS for Connection of EVB and EVA - ER No Adverse Comment	10	17-Apr-15	26-Apr-15	1																		
A5940	MS for Temporary Steel Tower under existing W/B Bridge - ER No Adverse Comment	2	15-Feb-15 A	21-Mar-15	54																		
A7580	MS Temporary Bridge TA2 - Resubmission	3	16-Mar-15 A	22-Mar-15	3																		
A7590	MS Temporary Bridge TA2 - ER No Adverse Comment	6	23-Mar-15	28-Mar-15	3																		
A8931	MS for installation of Temporary JTI sign gantry- Submission	0	10-Mar-15 A	15-Mar-15 A																			
A8941	MS for installation of Temporary JTI sign gantry - ER Review & Comment	0	16-Mar-15 A	19-Mar-15 A																			
A8951	MS for installation of Temporary JTI sign gantry - Resubmission	5	20-Mar-15	24-Mar-15	18																		
A8961	MS for installation of Temporary JTI sign gantry - ER No Adverse Comment	5	25-Mar-15	29-Mar-15	18																		
02.4 - Contractor's Design and Build Items																							
0240-1113	Noise Enclosure Structural - Shop Drawings	0	02-Jan-14 A	20-Mar-15	172																		
0240-1180	HGHK Permanent Carpark Design - ER/HGHK Review and Comment	80	20-Mar-15	07-Jun-15	32																		
0240-1270	Landscaping Design - Submission	90	20-Mar-15*	17-Jun-15	700																		
A5890	Temp Bridge "TA2" Design (Foundation & Structure) - ER No Adverse Comment	2	01-Dec-14 A	22-Mar-15	4																		
A5900	Temp Bridge "TA2" - Fabrication	2	01-Dec-14 A	22-Mar-15	4																		
A8991	Design for Trial Panels > Green Roof & Wall- ER No Adverse Comment	21	20-Mar-15	09-Apr-15	0																		
A9001	Design for Trial Panels > Green Roof & Wall - Fabrication	48	10-Apr-15	27-May-15	0																		
02.5 - Bridge Segment/Beam Off-site Precasting																							
0250-1720.19	Precast Beam Bridge C1 2021-C	4	26-Jan-15 A	23-Mar-15	292																		
0250-1720.20	Precast Beam Bridge C1 2122-A	18	11-Feb-15 A	06-Apr-15	278																		
0250-1720.21	Precast Beam Bridge C1 2122-B	18	12-Feb-15 A	06-Apr-15	278																		
0250-1720.22	Precast Beam Bridge C1 2122-C	18	12-Feb-15 A	06-Apr-15	45																		
0250-1720.23	Precast Beam Bridge C1 2122-D	18	07-Apr-15	24-Apr-15	242																		
0250-1720.25	Precast Beam Bridge C1 2122-E	18	25-Apr-15	12-May-15	242																		
0250-1720.26	Precast Beam Bridge C1 2122-F	18	13-May-15	30-May-15	242																		
0250-1720.27	Precast Beam Bridge E E3E2-A	18	20-Mar-15	06-Apr-15	45																		
0250-1720.28	Precast Beam Bridge E E3E2-B	18	07-Apr-15	24-Apr-15	45																		
0250-1720.29	Precast Beam Bridge E E3E2-C	18	25-Apr-15	12-May-15	45																		
0250-1720.30	Precast Beam Bridge E E4E3-A	18	13-May-15	30-May-15	45																		
0250-1720.31	Precast Beam Bridge E E4E3-B	18	31-May-15	17-Jun-15	45																		
0250-2070	Bridge F1C Pier 36 T-span Segment Off-site Casting (13 nos.)	31	20-Mar-15	19-Apr-15	263																		

Remaining Level of Effort ◆ ◆ Milestone
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

Contract HY/2009/19

Three Months Rolling Programme (20 March to 19 June 2015)

Page 1 of 10

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
						March			April			May			June																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
	0250-2080	Bridge F1C Pier 37 T-span Segment Off-site Casting (11 nos.)	27	20-Apr-15	16-May-15	263																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015															
						March				April				May				June			
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21
A3810	Tunnel Bay 20 -Tunnel Roof - (Concrete)	0	13-Mar-15 A	13-Mar-15 A		I Tunnel Bay 20 -Tunnel Roof - (Concrete)															
A3813	APS Bay 21 Col - (Reb. Fix + Concrete)	2	11-Mar-15 A	21-Mar-15	69	APS Bay 21 Col - (Reb. Fix + Concrete)															
A3990	Tunnel Bay 21 -Tunnel Roof - Steel Fixing	0	14-Feb-15 A	12-Mar-15 A		Tunnel Bay 21 -Tunnel Roof - Steel Fixing															
A4000	Tunnel Bay 21 -Tunnel Roof - (Concrete)	0	13-Mar-15 A	13-Mar-15 A		I Tunnel Bay 21 -Tunnel Roof - (Concrete)															
A4000.1	Tunnel Bay 21 -Tunnel Roof - Steel Fixing - Remaining Works	14	20-Mar-15	02-Apr-15	56	Tunnel Bay 21 -Tunnel Roof - Steel Fixing - Remaining Works															
A4000.2	Tunnel Bay 21 -Tunnel Roof - (Concrete) - Remaining Works	1	03-Apr-15	03-Apr-15	56	I Tunnel Bay 21 -Tunnel Roof - (Concrete) - Remaining Works															
A5414	APS Basement (Bay 21-North) - Staircase - Falseworks/Formworks	8	09-Mar-15 A	30-Mar-15	6	APS Basement (Bay 21-North) - Staircase - Falseworks/Formworks															
A5424	APS Basement (Bay 21-North) - Staircase - Rebar-Fixing + Concreting	14	30-Mar-15	18-Apr-15	6	APS Basement (Bay 21-North) - Staircase - Rebar-Fixing + Concreting															
A5425	APS Basement (Bay 21-North) - Partition wall	14	20-Mar-15	08-Apr-15	15	APS Basement (Bay 21-North) - Partition wall															
A5426	APS Basement (Bay 21-South) - Staircase - Falseworks/Formworks	12	18-Apr-15	04-May-15	6	APS Basement (Bay 21-South) - Staircase - Falseworks/Formworks															
A5427	APS Basement (Bay 21South) - Staircase - Rebar-Fixing + Concreting	14	04-May-15	20-May-15	8	APS Basement (Bay 21South) - Staircase - Rebar-Fixing + Concreting															
A5427.1	APS Basement (Bay 21-South) - Partition wall	14	18-Apr-15	06-May-15	6	APS Basement (Bay 21-South) - Partition wall															
A5427.2	APS Basement (Bay 20) - Partition wall	14	18-Apr-15	06-May-15	6	APS Basement (Bay 20) - Partition wall															
A5427.3	APS Basement (Bay 19) - Partition wall	14	06-May-15	22-May-15	6	APS Basement (Bay 19) - Partition wall															
A5427.4	APS Basement (Bay 18) - Partition wall	10	09-Mar-15 A	31-Mar-15	19	APS Basement (Bay 18) - Partition wall															
A5427.5	APS Basement (Bay 17) - Partition wall	10	09-Mar-15 A	31-Mar-15	47	APS Basement (Bay 17) - Partition wall															
A5427.6	BHW Coring at C15 & C19 Interface	0	06-Feb-15 A	02-Mar-15 A		W Coring at C15 & C19 Interface															
A5454	Vertical Saw Cutting of BHW @ 9M(H) X 32M(L)	3	03-Mar-15 A	23-Mar-15	5	Vertical Saw Cutting of BHW @ 9M(H) X 32M(L)															
A5465	Horizontal Saw Cutting of BHW @ 9M(H) X 32M(L)	8	16-Mar-15 A	28-Mar-15	0	Horizontal Saw Cutting of BHW @ 9M(H) X 32M(L)															
A5474	Removal of BHW Saw Cutted Blocks	10	30-Mar-15	13-Apr-15	0	Removal of BHW Saw Cutted Blocks															
A5484	Removal of BHW > Prepare CJ By Breaker Machine	4	14-Apr-15	17-Apr-15	0	Removal of BHW > Prepare CJ By Breaker Machine															
A5495.1	Complete In situ Stitch	5	18-Apr-15	23-Apr-15	0	Complete In situ Stitch															
A5496	Complete Centerwall	10	24-Apr-15	06-May-15	0	Complete Centerwall															
A5497	Complete OHVD	10	07-May-15	18-May-15	0	Complete OHVD															
A5498	Complete Tunnel Roof	10	19-May-15	29-May-15	0	Complete Tunnel Roof															
A5830	Completion of Outstanding Works at APS & Tunnel	0		29-May-15	0	◆ Completion of Outstanding Works															
05.1.4 - Tunnel Structure																					
A5393	Tunnel Bay 16 -Tunnel Roof - Steel Fixing	0	14-Feb-15 A	07-Mar-15 A		Tunnel Bay 16 -Tunnel Roof - Steel Fixing															
A5394	Tunnel Bay 16 -Tunnel Roof - (Concrete)	0	08-Mar-15 A	08-Mar-15 A		I Tunnel Bay 16 -Tunnel Roof - (Concrete)															
A5395	Weak Seam Rectification works for sub-standard D-Wall	8	10-Mar-15 A	30-Mar-15	48	Weak Seam Rectification works for sub-standard D-Wall															
A5396	Complete Tunnel Roof	0		20-Mar-15	0	◆ Complete Tunnel Roof															
05.1.5 - EVB Sub-structure & Tunnel																					
A10530	Tunnel Roadside/Profile Barrier and Cable Trough Portion IB & ID > Bay 14-16	14	20-Mar-15	08-Apr-15	1	Tunnel Roadside/Profile Barrier and Cable Trough Portion IB & ID > Bay 14-16															
A10540	Tunnel Roadside/Profile Barrier and Cable Trough Portion IB & ID > Bay 16-19	14	09-Apr-15	24-Apr-15	1	Tunnel Roadside/Profile Barrier and Cable Trough Portion IB & ID > Bay 16-19															
A5513	Tunnel Roadside/Profile Barrier and Cable Trough Portion IB & ID > Bay 19-21	14	25-Apr-15	12-May-15	1	Tunnel Roadside/Profile Barrier and Cable Trough Portion IB & ID > Bay 19-21															
A5514	Tunnel Roadside/Profile Barrier and Cable Trough Portion IVIIB & IXB	14	13-May-15	29-May-15	1	Tunnel Roadside/Profile Barrier and Cable Trough Portion IVIIB & IXB															
A5524	EVB Basement (Zone A1) - Partition Wall (Reb. Fix + Concreting) > CH4850-CH4875	14	07-Apr-15	22-Apr-15	74	EVB Basement (Zone A1) - Partition Wall (Reb. Fix + Concreting) > CH4850-CH4875															
A5534	EVB Basement (Zone A1) - Staircase-2nos.(Reb. Fix + Concreting) >CH4850-CH4875	14	23-Apr-15	09-May-15	130	EVB Basement (Zone A1) - Staircase-2nos.(Reb. Fix + Concreting) >CH4850-CH4875															
A5544	EVB Basement (Zone A2) - Partition Wall (Reb. Fix + Concreting)> CH4875-CH4900	14	11-May-15	26-May-15	130	EVB Basement (Zone A2) - Partition Wall (Reb. Fix + Concreting)> CH4875-CH4900															
A5554	EVB Basement (Zone A2) - Staircase-1nos.(Reb. Fix + Concreting)> CH4875-CH4900	14	27-May-15	11-Jun-15	130	EVB Basement (Zone A2) - Staircase-1nos.(Reb. Fix + Concreting)> CH4875-CH4900															
A5564	EVB Basement (Zone B1) - Partition Wall (Reb. Fix + Concreting)> CH4900-CH4920	14	12-Jun-15	29-Jun-15	130	EVB Basement (Zone B1) - Partition Wall (Reb. Fix + Concreting)> CH4900-CH4920															
A5744	EVB Mezzanine (Zone A1) - (Reb. Fix + Concreting)> CH4850-CH4875	14	23-Apr-15	09-May-15	74	EVB Mezzanine (Zone A1) - (Reb. Fix + Concreting)> CH4850-CH4875															
A5754	EVB Mezzanine (Zone A1) - Staircase-2nos.(Reb. Fix + Concreting)> CH4850-CH4875	14	11-May-15	26-May-15	74	EVB Mezzanine (Zone A1) - Staircase-2nos.(Reb. Fix + Concreting)> CH4850-CH4875															
A5764	EVB Mezzanine (Zone A2) - (Reb. Fix + Concreting)> CH4875-CH4900	14	27-May-15	11-Jun-15	74	EVB Mezzanine (Zone A2) - (Reb. Fix + Concreting)> CH4875-CH4900															
A5784	EVB Mezzanine (Zone B1) - Partition Wall (Reb. Fix + Concreting)> CH4900-CH4920	14	12-Jun-15	29-Jun-15	74	EVB Mezzanine (Zone B1) - Partition Wall (Reb. Fix + Concreting)> CH4900-CH4920															
05.2 - Cut & Cover Tunnel Ch 4932-5149																					
05.2.3 - ELS																					
A10400	Tunnel Bay 1 & 2 Duct room wall steam	7	13-Mar-15 A	26-Mar-15	64	Tunnel Bay 1 & 2 Duct room wall steam															
A4192	Pump Sump E - Storm Water Room Collection	7	20-Mar-15	26-Mar-15	64	Pump Sump E - Storm Water Room Collection															

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015																	
						March				April				May				June					
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21		
05.2.4 - Tunnel Structure																							
0524-2535	Waterproof Top Slab Bay 1 to Bay 4	2	20-Mar-15	21-Mar-15	117	Waterproof Top Slab Bay 1 to Bay 4																	
05.2.5 - Road & Miscellaneous Works																							
0525-2882	Backfill above Tunnel Structure Bay 1 to Bay 4	5	23-Mar-15	27-Mar-15	117	Backfill above Tunnel Structure Bay 1 to Bay 4																	
0525-2900	Tunnel Roadside/Profile Barrier (excl vent bldg)	27	05-Aug-14 A	15-Apr-15	44	Tunnel Roadside/Profile Barrier (excl vent bldg)																	
0525-2940	Backfill above Tunnel Structure Bay 5 to Bay 9	0	28-Nov-14 A	17-Mar-15 A		Backfill above Tunnel Structure Bay 5 to Bay 9																	
A10410	Paving Bay 13 - 5	0	16-Feb-15 A	19-Mar-15 A		Paving Bay 13 - 5																	
A10420	Paving Bay 4 - 1	3	26-Mar-15	28-Mar-15	151	Paving Bay 4 - 1																	
A10430	Drainage Bay 13 - 5	0	23-Feb-15 A	16-Mar-15 A		Drainage Bay 13 - 5																	
A10440	Drainage Bay 4 - 1	14	23-Mar-15	05-Apr-15	1631	Drainage Bay 4 - 1																	
A10450	Provisioning of Carwash Machine - Temp FEHD	10	20-Mar-15	31-Mar-15	114	Provisioning of Carwash Machine - Temp FEHD																	
A10460	Road & Carpark Marking - Temp. FEHD	5	18-Mar-15 A	07-Apr-15	123	Road & Carpark Marking - Temp. FEHD																	
A10470	Lighting - Temp FEHD	5	20-Mar-15	25-Mar-15	119	Lighting - Temp FEHD																	
A10480	Portal Wall at top of tunnel	0	09-Feb-15 A	25-Feb-15 A		Portal Wall at top of tunnel																	
A10527	Remove Tunnel Falseworks Bay 14-16	7	20-Mar-15	27-Mar-15	8	Remove Tunnel Falseworks Bay 14-16																	
A10528	Remove Tunnel Falseworks Bay 16-19	7	24-Mar-15	31-Mar-15	16	Remove Tunnel Falseworks Bay 16-19																	
A10529	Remove Tunnel Falseworks Bay 19-21	7	27-Mar-15	07-Apr-15	16	Remove Tunnel Falseworks Bay 19-21																	
A10589.2	Remedial Works - Bay 9 OHVD - WestBound	10	20-Mar-15	31-Mar-15	47	Remedial Works - Bay 9 OHVD - WestBound																	
A10589.6	Remedial Works - Concrete Repair Works > Honeycombs/laitance, etc.	2	09-Mar-15 A	21-Mar-15	43	Remedial Works - Concrete Repair Works > Honeycombs/laitance, etc.																	
A10589.7	Waterproofing of D-Walls Bay 1-13	10	20-Mar-15	31-Mar-15	43	Waterproofing of D-Walls Bay 1-13																	
A10589.8	Waterproofing of D-Walls Bay 14-21	14	20-Mar-15	08-Apr-15	43	Waterproofing of D-Walls Bay 14-21																	
A10590	Complete Remaining work at C/C Tunnel	0		08-Apr-15	43	Complete Remaining work at C/C Tunnel																	
06 - SECTION 3 OF THE WORKS																							
06.2 - Box Culvert U1																							
A9180	In-Situ Testing of Drainage Pipe	7	19-Jan-15 A	27-Mar-15	37	In-Situ Testing of Drainage Pipe																	
06.3 - Admin Building																							
0630-3119.24	Grd. Beam - (GL > G2-K6) - Rebar Fixing (Grd. Beam & Pile Cap)	1	03-Mar-15 A	20-Mar-15	47	Grd. Beam - (GL > G2-K6) - Rebar Fixing (Grd. Beam & Pile Cap)																	
0630-3119.25	Grd. Beam - (GL > G2-K6) - Erect Formworks (Grd. Beam & Pile Cap)	6	20-Mar-15	27-Mar-15	47	Grd. Beam - (GL > G2-K6) - Erect Formworks (Grd. Beam & Pile Cap)																	
0630-3119.26	Grd. Beam - (GL > G2-K6) - Concreting (Grd. Beam & Pile Cap)	1	27-Mar-15	28-Mar-15	47	Grd. Beam - (GL > G2-K6) - Concreting (Grd. Beam & Pile Cap)																	
0630-3119.27	Grd. Beam - (GL > G2-K6) - Formworks, sheet-Pile Removal and Backfill	5	28-Mar-15	07-Apr-15	47	Grd. Beam - (GL > G2-K6) - Formworks, sheet-Pile Removal and Backfill																	
0630-3119.84	Grd. Beam - (GL > A1-B6) - Install Capping Plate	0	06-Mar-15 A	20-Mar-15	27	Grd. Beam - (GL > A1-B6) - Install Capping Plate																	
0630-3119.85	Grd. Beam - (GL > A1-B6) - Rebar Fixing (Grd. Beam & Pile Cap) + Formworks	6	20-Mar-15	26-Mar-15	27	Grd. Beam - (GL > A1-B6) - Rebar Fixing (Grd. Beam & Pile Cap) + Formworks																	
0630-3119.86	Grd. Beam - (GL > A1-B6) - Concreting (Grd. Beam & Pile Cap)	7	27-Mar-15	02-Apr-15	35	Grd. Beam - (GL > A1-B6) - Concreting (Grd. Beam & Pile Cap)																	
0630-3119.87	Grd. Beam - (GL > A1-B6) - Formworks, Sheet-Pile Removal and Backfill	6	02-Apr-15	13-Apr-15	26	Grd. Beam - (GL > A1-B6) - Formworks, Sheet-Pile Removal and Backfill																	
0630-3121.49	Grd. Beam - (GL > P3-R6) - Back Fill	0	07-Feb-15 A	06-Mar-15 A		Grd. Beam - (GL > P3-R6) - Back Fill																	
08 - SECTION 5 WORK																							
08.1 - Retaining Wall 'F' Substructure																							
A7671	Retaining Wall F Pre-Bored H-Pile - H - Beam + Grout > BS40a	0	07-Feb-15 A	04-Mar-15 A		Retaining Wall F Pre-Bored H-Pile - H - Beam + Grout > BS40a																	
A7672	Retaining Wall F Pre-Bored H-Pile - H - Beam + Grout > BS40b	0	30-Jan-15 A	06-Mar-15 A		Retaining Wall F Pre-Bored H-Pile - H - Beam + Grout > BS40b																	
A7673	Retaining Wall F Pre-Bored H-Pile - H - Beam + Grout > BS41a	0	04-Feb-15 A	06-Mar-15 A		Retaining Wall F Pre-Bored H-Pile - H - Beam + Grout > BS41a																	
A7740.1	Retaining Wall F Pre-Bored H-Pile - H - Installing H-Pile > BS45a	0	31-Dec-14 A	24-Feb-15 A		Retaining Wall F Pre-Bored H-Pile - H - Installing H-Pile > BS45a																	
A7740.2	Retaining Wall F Pre-Bored H-Pile - H - Extract H-Pile due to Collapse of soil > BS45a	0	25-Feb-15 A	03-Mar-15 A		Retaining Wall F Pre-Bored H-Pile - H - Extract H-Pile due to Collapse of soil > BS45a																	
A7740.3	Retaining Wall F Pre-Bored H-Pile - H - Grout plug > BS45a	0	04-Mar-15 A	06-Mar-15 A		Retaining Wall F Pre-Bored H-Pile - H - Grout plug > BS45a																	
A7740.4	Retaining Wall F Pre-Bored H-Pile - H - Beam + Grout > BS45a	5	06-Mar-15 A	25-Mar-15	331	Retaining Wall F Pre-Bored H-Pile - H - Beam + Grout > BS45a																	
A7791	Retaining Wall F Pre Bored - H > Pile Testing	18	26-Mar-15	18-Apr-15	331	Retaining Wall F Pre Bored - H > Pile Testing																	
A7792.1	Construction of pile cap for Retaining Wall F > C4-1	8	20-Apr-15	28-Apr-15	331	Construction of pile cap for Retaining Wall F > C4-1																	
A7792.2	Construction of pile cap for Retaining Wall F > C4-2	8	29-Apr-15	08-May-15	331	Construction of pile cap for Retaining Wall F > C4-2																	
A7792.3	Construction of pile cap for Retaining Wall F > C5-1	8	09-May-15	18-May-15	331	Construction of pile cap for Retaining Wall F > C5-1																	
A7792.4	Construction of pile cap for Retaining Wall F > C5-2	8	19-May-15	27-May-15	331	Construction of pile cap for Retaining Wall F > C5-2																	

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015															
						March				April				May				June			
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21
A7792.5	Construction of pile cap for Retaining Wall F > C5-3	8	28-May-15	05-Jun-15	331																
A7792.6	Construction of pile cap for Retaining Wall F > C5-4	8	06-Jun-15	15-Jun-15	331																
A7800	Complete Pre-Bored H-Pile > Retaining Wall	0		25-Mar-15	331																
09 - SECTION 6 OF THE WORKS																					
09.2 - Westbound - Pier 26-27																					
0920-2110	Pier 26-2 Pre-Bored H-Piles	6	07-Feb-15 A	26-Mar-15	145																
0920-2111	Pier 26-1 Pre-Bored H-Piles	8	09-Mar-15 A	30-Mar-15	145																
0920-2112	Pier 26-3 Pre-Bored H-Piles	12	30-Mar-15	16-Apr-15	145																
0920-2113	Pier 26-4 Pre-Bored H-Piles	12	16-Apr-15	30-Apr-15	145																
10 - SECTION X OF THE WORKS																					
10.1 - E/B Bridges (Bridge D, E and F)																					
10.1.1 - Marine Pier Construction																					
Pier F01 to F02																					
1011-2900	F1B Pier/Column Construction	12	20-Mar-15	02-Apr-15	617																
1011-2910	F1B Crosshead Construction	18	07-Apr-15	27-Apr-15	617																
1011-2930	Bearing installation pier F1B/F2B	12	28-Apr-15	12-May-15	617																
10.1.3 - E/B Bridge Construction																					
All E/B Bridges (Common)																					
1013-1720	Permanent Noise Barrier Type B1 E/B Bridge Ch 962-1059 (132m)	0	02-Dec-14 A	09-Mar-15 A																	
1013-1730	Permanent Noise Barrier Type A1 E/B Bridge Ch 826-962 (136m)	0	05-Dec-14 A	17-Mar-15 A																	
A7621	Remaining E/B Bridges Bitumin Paving Works + Marking - Bridge D1 & D2	0	18-Mar-15 A	19-Mar-15 A																	
10.1.4 - Bridge E / Hing Fat Slip Road																					
Bridge Construction																					
A9260	Bridge E (Pier 18-19) - Rebar Fix > Diaphragm + Slab + Pipe install	0	13-Feb-15 A	26-Feb-15 A																	
A9270	Bridge E (Pier 18-19) - Formworks > Slab	0	26-Feb-15 A	26-Feb-15 A																	
A9280	Bridge E (Pier 18-19) - Concreting > Diaphram + Slab	0	27-Feb-15 A	27-Feb-15 A																	
A9310	Bridge E (Pier 18-19) - Stitching > Reb. Fix + Concretin	0	20-Feb-15 A	16-Mar-15 A																	
A9360	Bridge E (Pier 17 - 18) - Rebar Fix > Diaphragm + Slab + Pipe install	0	17-Feb-15 A	02-Mar-15 A																	
A9370	Bridge E (Pier 17 - 18) - Formworks > Slab	0	02-Mar-15 A	02-Mar-15 A																	
A9380	Bridge E (Pier 17 - 18) - Concreting > Diaphram + Slab	0	03-Mar-15 A	03-Mar-15 A																	
A9400	Bridge E (Pier 17 - 18) - Stitching > Reb. Fix + Concretin	0	17-Feb-15 A	16-Mar-15 A																	
A9450	Bridge E (Pier 19 - D1) - Rebar Fix > Diaphragm + Slab + Pipe install	0	18-Feb-15 A	07-Mar-15 A																	
A9460	Bridge E (Pier 19 - D1) - Formworks > Slab	0	07-Mar-15 A	07-Mar-15 A																	
A9470	Bridge E (Pier 19 - D1) - Concreting > Diaphram + Slab	0	09-Mar-15 A	09-Mar-15 A																	
A9472	Bridge E (Pier E1 - D1) - Temporary L3 Parapet Railings	0	18-Feb-15 A	13-Mar-15 A																	
A9500	Bridge E (Pier 16 - 19) - Lightings	1	24-Feb-15 A	20-Mar-15	1																
A9510	Bridge E (Pier 17 - 19) - MJ	1	18-Mar-15 A	21-Mar-15	0																
A9520	Bridge E (Pier 17 - 19) - install pre-cast Parapet	0	06-Mar-15 A	18-Mar-15 A																	
A9521	Bridge E (Pier 17 - 19) - Instatall L3 Railing/Parapet	1	18-Mar-15 A	20-Mar-15	7																
A9540	Bridge E (Pier 17 - D1) - Drainage Gully	0	16-Mar-15 A	20-Mar-15	1																
A9560	Bridge E (Pier 19 - D1) - Parapet	14	30-Mar-15	17-Apr-15	789																
A9561	Bridge E (Pier 19 - D1) - Noise Barrier > Post + Panel	14	18-Apr-15	05-May-15	789																
A9570	Bridge E (Pier 19 - D1) - Green Wall	2	06-May-15	08-May-15	789																
A9590	Bridge E (Pier D1) - MJ	2	17-Mar-15 A	21-Mar-15	4																
A9600	Bridge E (Pier 17 - D1) - Asphalting	5	21-Mar-15	26-Mar-15	0																
A9610	Bridge E (Pier 17 - D1) - Road Marking	4	23-Mar-15	27-Mar-15	0																
A9620	Bridge E (Pier 17 - D1) - Signage	5	20-Mar-15	25-Mar-15	2																
10.2 - W/B Bridges (Bridge C and F)																					
10.2.2 - Bridge Construction																					

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 March to 19 June 2015)

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015															
						March			April				May				June				
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21
All W/B Bridges (Common)																					
A11770	Decommissioning of Exis. Fire mains & Fire Hyd. at Meddian Barrier	3	30-Mar-15	01-Apr-15	11	Decommissioning of Exis. Fire mains & Fire Hyd. at Meddian Barrier															
A11780	Installation of New Fire Mains	7	30-Mar-15	09-Apr-15	7	Installation of New Fire Mains															
A11790	Install Temporary Lighting at Existing E/B Bridge	5	30-Mar-15	07-Apr-15	9	Install Temporary Lighting at Existing E/B Bridge															
A11800	Installation of Temporary L3 Railings	5	11-Apr-15	17-Apr-15	0	Installation of Temporary L3 Railings															
A11810	Install Traffic Signage	1	16-Apr-15	17-Apr-15	0	Install Traffic Signage															
A8060	Saw Cutting/Opening of Median Barrier at Existing W/B bridge > (Pier 15-21 & 44-49)	13	30-Mar-15	11-Apr-15	0	Saw Cutting/Opening of Median Barrier at Existing W/B bridge > (Pier 15-21 & 44-49)															
A8061	Opening of Median Barrier > (Pier 15-21 & 44-49) - Paving + Rd. marking	6	12-Apr-15	17-Apr-15	0	Opening of Median Barrier > (Pier 15-21 & 44-49) - Paving + Rd. marking															
A8061.1	Saw - Cutting of Slab at W/B Bridge (Pier 26-44) - Along Meddian Beams - Part 1	23	15-Nov-14 A	18-Apr-15	10	Saw - Cutting of Slab at W/B Bridge (Pier 26-44) - Along Meddian Beams - Part 1															
A8530	Saw - Cutting of Slab at W/B Bridge (Pier 26-44) - Remaining Area - Part 2	13	20-Apr-15	02-May-15	12	Saw - Cutting of Slab at W/B Bridge (Pier 26-44) - Remaining Area															
A8540	Saw - Cutting of Slab at W/B Bridge (Pier 17-26)	7	03-May-15	09-May-15	102	Saw - Cutting of Slab at W/B Bridge (Pier 17-26)															
A9820.1	Erection of Fixed Gantry - Erect Main Structure > Pier 34-35	10	20-Apr-15	30-Apr-15	105	Erection of Fixed Gantry - Erect Main Structure > Pier 34-35															
A9820.2	Erection of Fixed Gantry - Erect Cantilever Structure > Pier 34-35	10	02-May-15	13-May-15	105	Erection of Fixed Gantry - Erect Cantilever Structure >															
A9820.3	Erection of Fixed Gantry - miscellaneous Parts & Support > Pier 34-35	10	14-May-15	25-May-15	105	Erection of Fixed Gantry - miscellaneous															
10.3 - Middle Bridge (Bridge F)																					
10.3.1 - Pier Construction																					
Abutment D12																					
1031-1058	Abut D12 (Approach Ramp Area) - Reb Fix + Concrete Pour 3	7	27-Dec-14 A	27-Mar-15	72	Abut D12 (Approach Ramp Area) - Reb Fix + Concrete Pour 3															
A10720	Construct Abutment D12 Existing W/B & E/B Bridge - Excav. Bored Pile (4 nos)	0	13-Mar-15 A	16-Mar-15 A		Construct Abutment D12 Existing W/B & E/B Bridge - Excav. Bored Pile (4 nos)															
A10730	Construct Abutment D12 W/B Bridge - Prepare CJ	10	20-Mar-15	31-Mar-15	147	Construct Abutment D12 W/B Bridge - Prepare CJ															
A10740	Construct Abutment D12 - Construct Abut D12 Pile Cap + Backfill	14	01-Apr-15	20-Apr-15	147	Construct Abutment D12 - Construct Abut D12 Pile Cap + Backfill															
10.4 - Bridge Deck Demolition																					
10.4.1 - Existing W/B Bridge (Part 1)																					
A6340	Demolish W/B Bridge Deck Pier 28-29 (7 beams) > by Crane - A	14	02-May-15	19-May-15	10	Demolish W/B Bridge Deck Pier 28-29 (7 beams) > by Crane - A															
A6350	Demolish W/B Bridge Deck Pier 29-30 (7 beams) > by Crane - A	7	19-May-15	27-May-15	10	Demolish W/B Bridge Deck Pier 29-30 (7 beams) > by Crane - A															
A6360	Demolish W/B Bridge Deck Pier 30-31 (7 beams) > by Crane - A	14	19-May-15	04-Jun-15	11	Demolish W/B Bridge Deck Pier 30-31 (7 beams) > by Crane - A															
A6370	Demolish W/B Bridge Deck Pier 31-32 (7 beams) > by Crane - A	7	27-May-15	04-Jun-15	10	Demolish W/B Bridge Deck Pier 31-32 (7 beams) > by Crane - A															
A6380	Demolish W/B Bridge Deck Pier 32-33 (7 beams) > by Crane - A	14	27-May-15	12-Jun-15	10	Demolish W/B Bridge Deck Pier 32-33 (7 beams) > by Crane - A															
A6390	Demolish W/B Bridge Deck Pier 33-34 (7 beams) > by Crane - A	7	04-Jun-15	12-Jun-15	10	Demolish W/B Bridge Deck Pier 33-34 (7 beams) > by Crane - A															
A6400	Demolish W/B Bridge Pier 29 > by Crane - B	10	27-May-15	08-Jun-15	16	Demolish W/B Bridge Pier 29 > by Crane - B															
A6400.1	Demolish W/B Bridge Pier 29 - Pile Cap	14	08-Jun-15	25-Jun-15	16	Demolish W/B Bridge Pier 29 - Pile Cap															
A6420	Demolish W/B Bridge Pier 30 > by Crane - B	10	04-Jun-15	16-Jun-15	16	Demolish W/B Bridge Pier 30 > by Crane - B															
A6420.2	Demolish W/B Bridge Pier 33 > by Crane - B	10	12-Jun-15	25-Jun-15	10	Demolish W/B Bridge Pier 33 > by Crane - B															
A6631	Erect/Assemble LG1 + T&C > Erect Leg Support At Pier 41-44	6	20-Apr-15	25-Apr-15	0	Erect/Assemble LG1 + T&C > Erect Leg Support At Pier 41-44															
A6632	Erect/Assemble LG1 + T&C > Istall Main Beam/Girder Support - Middle Span at Bay 42 - 43	14	25-Apr-15	13-May-15	0	Erect/Assemble LG1 + T&C > Istall Main Beam/Girder Support - Middle Span at Bay 42 - 43															
A6633	Erect/Assemble LG1 + T&C > Istall Main Beam/Girder Support - End Span at Bay 43 - 44	14	13-May-15	29-May-15	0	Erect/Assemble LG1 + T&C > Istall Main Beam/Girder Support - End Span at Bay 43 - 44															
A6634	Erect/Assemble LG1 + T&C > Istall Main Beam/Girder Support - End Span at bay 41 - 42	14	13-May-15	29-May-15	0	Erect/Assemble LG1 + T&C > Istall Main Beam/Girder Support - End Span at bay 41 - 42															
A6635	Erect/Assemble LG1 + T&C > Istall Mounting Support & Cables	10	29-May-15	10-Jun-15	0	Erect/Assemble LG1 + T&C > Istall Mounting Support & Cables															
A6636	Erect/Assemble LG1 + T&C > Istall Miscellaneous Parts & support	8	10-Jun-15	19-Jun-15	0	Erect/Assemble LG1 + T&C > Istall Miscellaneous Parts & support															
A6650	Demolish W/B Bridge Deck Pier 43 to 44 (6 beams) > by LG1	6	19-Jun-15	27-Jun-15	0	Demolish W/B Bridge Deck Pier 43 to 44 (6 beams) > by LG1															
A8079.1	Pier 28 Erect Falsework at existing W/B Bridge prior to demolition	6	20-Mar-15	26-Mar-15	38	Pier 28 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.11	Pier 29 Erect Falsework at existing W/B Bridge prior to demolition	6	27-Mar-15	02-Apr-15	46	Pier 29 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.12	Pier 30 Erect Falsework at existing W/B Bridge prior to demolition	0	26-Feb-15 A	07-Mar-15 A		Pier 30 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.14	Pier 32 Erect Falsework at existing W/B Bridge prior to demolition	6	07-Apr-15	13-Apr-15	47	Pier 32 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.15	Pier 33 Erect Falsework at existing W/B Bridge prior to demolition	4	11-Mar-15 A	25-Mar-15	66	Pier 33 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.16	Pier 34 Erect Falsework at existing W/B Bridge prior to demolition	6	14-Apr-15	20-Apr-15	48	Pier 34 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.18	Pier 27 Erect Falsework at existing W/B Bridge prior to demolition	0	09-Mar-15 A	16-Mar-15 A		Pier 27 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.19	Pier 26 Erect Falsework at existing W/B Bridge prior to demolition	0	04-Mar-15 A	09-Mar-15 A		Pier 26 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.2	Pier 25 Erect Falsework at existing W/B Bridge prior to demolition	6	21-Apr-15	27-Apr-15	104	Pier 25 Erect Falsework at existing W/B Bridge prior to demolition															
A8079.21	Pier 24 Erect Falsework at existing W/B Bridge prior to demolition	6	27-Apr-15	04-May-15	104	Pier 24 Erect Falsework at existing W/B Bridge prior to demolition															

Remaining Level of Effort

 Milestone

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Contract HY/2009/19

Three Months Rolling Programme (20 March to 19 June 2015)

Page 6 of 10

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015															
						March				April				May				June			
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21
A11350	TA2-(Pier TA24-25) > Intall Bearing	4	17-Apr-15	22-Apr-15	14																
A11360	TA2-(Pier TA24-25) > Main Beam Fabrication (TA24-25)	6	10-Apr-15	17-Apr-15	19																
A11370	TA2-(Pier TA24-25) > Main Beam Erection	1	22-Apr-15	23-Apr-15	14																
A11380	TA2-(Pier TA24-25) > Install Bondeck	6	23-Apr-15	30-Apr-15	14																
A11390	TA2-(Pier TA24-25) > Deck Rebar Fixing	6	30-Apr-15	08-May-15	14																
A11400	TA2-(Pier TA24-25) > Holding Down Bolts for L3 Railings	2	07-May-15	09-May-15	14																
A11410	TA2-(Pier TA24-25) > Deck Concreting	1	09-May-15	11-May-15	14																
A11420	TA2-(Pier TA24-25) > L3 Railings	3	11-May-15	14-May-15	14																
A11430	TA2-(Pier TA25-26) > Install TA26 Tower	1	30-Mar-15	31-Mar-15	2																
A11440	TA2-(Pier TA25-26) > Intall Scaffolding at TA26	3	31-Mar-15	07-Apr-15	20																
A11450	TA2-(Pier TA25-26) > TA23 Grouting	3	07-Apr-15	10-Apr-15	20																
A11460	TA2-(Pier TA25-26) > Intall Bearing	4	10-Apr-15	15-Apr-15	20																
A11470	TA2-(Pier TA25-26) > Main Beam Fabrication (TA25-26)	6	31-Mar-15	10-Apr-15	25																
A11480	TA2-(Pier TA25-26) > Main Beam Erection	1	15-Apr-15	16-Apr-15	20																
A11490	TA2-(Pier TA25-26) > Install Bondeck	6	16-Apr-15	23-Apr-15	20																
A11500	TA2-(Pier TA25-26) > Deck Rebar Fixing	6	23-Apr-15	30-Apr-15	20																
A11510	TA2-(Pier TA25-26) > Holding Down Bolts for L3 Railings	2	29-Apr-15	02-May-15	20																
A11520	TA2-(Pier TA25-26) > Deck Concreting	1	02-May-15	04-May-15	20																
A11530	TA2-(Pier TA25-26) > L3 Railings	3	04-May-15	07-May-15	20																
A11540	TA2-(Pier TA26-27) > Install TA27 Tower	1	23-Mar-15	24-Mar-15	2																
A11550	TA2-(Pier TA26-27) > Intall Scaffolding at TA27	3	24-Mar-15	27-Mar-15	26																
A11560	TA2-(Pier TA26-27) > TA23 Grouting	3	27-Mar-15	31-Mar-15	26																
A11570	TA2-(Pier TA26-27) > Intall Bearing	4	31-Mar-15	08-Apr-15	26																
A11580	TA2-(Pier TA26-27) > Main Beam Fabrication (TA26-27)	6	24-Mar-15	31-Mar-15	30																
A11590	TA2-(Pier TA26-27) > Main Beam Erection	1	08-Apr-15	09-Apr-15	26																
A11600	TA2-(Pier TA26-27) > Install Bondeck	6	09-Apr-15	16-Apr-15	26																
A11610	TA2-(Pier TA26-27) > Deck Rebar Fixing	6	16-Apr-15	23-Apr-15	26																
A11620	TA2-(Pier TA26-27) > Holding Down Bolts for L3 Railings	2	22-Apr-15	24-Apr-15	26																
A11630	TA2-(Pier TA26-27) > Deck Concreting	1	24-Apr-15	25-Apr-15	26																
A11640	TA2-(Pier TA26-27) > L3 Railings	3	25-Apr-15	29-Apr-15	26																
A11640.1	TA2-(Pier TA27-28) > Preparation works for R.C Wall	6	20-Mar-15	26-Mar-15	0																
A11640.2	TA2-(Pier TA27-28) > Formawork on R.C Wall	2	27-Mar-15	28-Mar-15	0																
A11640.3	TA2-(Pier TA27-28) > Rebar Fixing on R.C Wall	3	30-Mar-15	01-Apr-15	0																
A11640.4	TA2-(Pier TA27-28) > Concreting on R.C Wall	1	02-Apr-15	02-Apr-15	1																
A11640.5	TA2-(Pier TA27-28) > Waterproofing for Tunnel Roof	4	31-Mar-15	07-Apr-15	0																
A11640.6	TA2-(Pier TA27-28) > Soil Backfill to Ground Level	10	08-Apr-15	18-Apr-15	0																
A11640.7	TA2-(Pier TA27-28) > Formwork on TA28	2	20-Apr-15	21-Apr-15	0																
A11640.8	TA2-(Pier TA27-28) > Rebar Fixing on TA28	2	22-Apr-15	23-Apr-15	0																
A11640.9	TA2-(Pier TA27-28) > Install Holding Down Bolts on TA28	1	24-Apr-15	24-Apr-15	0																
A11640.91	TA2-(Pier TA27-28) > Concreting on TA28	1	25-Apr-15	25-Apr-15	0																
A11650	TA2-(Pier TA27-28) > Installation of TA28 Tower	1	27-Apr-15	27-Apr-15	0																
A11660	TA2-(Pier TA27-28) > Intall Scaffolding at TA28	3	28-Apr-15	30-Apr-15	0																
A11670	TA2-(Pier TA27-28) > TA28 Grouting	3	02-May-15	05-May-15	0																
A11680	TA2-(Pier TA27-28) > Intall Bearing	4	06-May-15	09-May-15	0																
A11690	TA2-(Pier TA27-28) > Main Beam Fabrication (TA27-28)	6	28-Apr-15	05-May-15	5																
A11700	TA2-(Pier TA27-28) > Main Beam Erection	1	11-May-15	11-May-15	0																
A11710	TA2-(Pier TA27-28) > Install Bondeck	6	12-May-15	18-May-15	0																
A11720	TA2-(Pier TA27-28) > Deck Rebar Fixing	6	19-May-15	25-May-15	0																
A11730	TA2-(Pier TA27-28) > Holding Down Bolts for L3 Railings	2	25-May-15	26-May-15	0																

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 March to 19 June 2015)

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015																	
						March				April				May				June					
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21		
A11740	TA2-(Pier TA27-28) > Deck Concreting	1	27-May-15	27-May-15	0																	■ TA2-(Pier TA27-28) > Deck Concreting	
A11750	TA2-(Pier TA27-28) > L3 Railings	3	28-May-15	30-May-15	0																	■ TA2-(Pier TA27-28) > L3 Railings	
A11760	Complete Temporary "TA2" Bridge	0		30-May-15	0																	◆ Complete Temporary "TA2" Bridge	
10.5.2 - Temporary Bridge 'TB'																							
A10280	TB > (Pier 16-17) - Stitching	0	02-Mar-15 A	02-Mar-15 A																		> (Pier 16-17) - Stitching	
A10290	TB > (Pier TB1-16) - L3 Railing Installation	0	03-Mar-15 A	06-Mar-15 A																		TB > (Pier TB1-16) - L3 Railing Installation	
A10300	Bridge E (Pier 16) - MJ	2	17-Mar-15 A	21-Mar-15	0																	■ Bridge E (Pier 16) - MJ	
A2480	TB > (Pier TB1-16) - L3 Railing Installation	0	06-Mar-15 A	09-Mar-15 A																		■ TB > (Pier TB1-16) - L3 Railing Installation	
10.6 - Tunnel Approach Ramp																							
10.6.1 - Approach Ramp (Excluding Portion IIB)																							
Bored Piles																							
A5851	Bored Pile Ramp - BN25	0	10-Feb-15 A	25-Feb-15 A																		Bored Pile Ramp - BN25	
A5853	Bored Pile Ramp - BM08	14	08-May-15	23-May-15	135																	Bored Pile Ramp - BM08	
A5856	Bored Pile Ramp > LHR- BN32	14	20-Mar-15	08-Apr-15	187																	Bored Pile Ramp > LHR- BN32	
A5857	Bored Pile Ramp > LHR - BN34	14	20-Mar-15	08-Apr-15	209																	Bored Pile Ramp > LHR - BN34	
A5858	Bored Pile Ramp - BM07	14	01-Apr-15	20-Apr-15	135																	Bored Pile Ramp - BM07	
A5859.21	Bored Pile Ramp - BN20	0	17-Feb-15 A	11-Mar-15 A																		Bored Pile Ramp - BN20	
A5859.22	Bored Pile Ramp - BN21	10	13-Mar-15 A	31-Mar-15	135																	Bored Pile Ramp - BN21	
A5859.24	Bored Pile Ramp - BS21	0	26-Feb-15 A	14-Mar-15 A																		Bored Pile Ramp - BS21	
A5859.26	Bored Pile Ramp - BS14	14	25-Apr-15	12-May-15	145																	Bored Pile Ramp - BS14	
A5859.27	Bored Pile Ramp - BS15	14	09-Apr-15	24-Apr-15	145																	Bored Pile Ramp - BS15	
A5859.28	Bored Pile Ramp - BS16	14	20-Mar-15	08-Apr-15	145																	Bored Pile Ramp - BS16	
A5859.29	Bored Pile Ramp - BM04	14	25-May-15	09-Jun-15	135																	Bored Pile Ramp - BM04	
A5859.3	Bored Pile Ramp - BM05	14	13-May-15	28-May-15	145																	Bored Pile Ramp - BM05	
A5859.31	Bored Pile Ramp - BM06	14	21-Apr-15	07-May-15	135																	Bored Pile Ramp - BM06	
A5859.32	Bored Pile Ramp > LHR - BN14	14	09-Apr-15	24-Apr-15	195																	Bored Pile Ramp > LHR - BN14	
A5859.33	Bored Pile Ramp > LHR - BN15	14	09-Apr-15	24-Apr-15	209																	Bored Pile Ramp > LHR - BN15	
A5859.34	Bored Pile Ramp > LHR - BN16	14	25-Apr-15	12-May-15	195																	Bored Pile Ramp > LHR - BN16	
A5859.35	Bored Pile Ramp > LHR - BN17	14	25-Apr-15	12-May-15	209																	Bored Pile Ramp > LHR - BN17	
A5859.36	Bored Pile Ramp > LHR - BN18	14	13-May-15	28-May-15	195																	Bored Pile Ramp > LHR - BN18	
A5859.36.1	Complete Bored Piles > LHR	0		28-May-15	195																	◆ Complete Bored Piles > LHR	
A5859.37	Complete Bored Piles Excl.Portion IIB	0		09-Jun-15	135																	◆ Complete Bored Piles Excl.Portion IIB	
A8050	Complete Pre-Bored H-Pile > CSD Approach Ramp	0		20-Mar-15	187																	◆ Complete Pre-Bored H-Pile > CSD Approach Ramp	
ELS																							
1061-1065	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D12 Northern Side	14	13-May-15	28-May-15	195																	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D12 Northern Side	
1061-1065.2	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D10 Northern Side	14	29-May-15	13-Jun-15	195																	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D10 Northern Side	
1061-1065.3	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D10-D09 Northern Side	14	15-Jun-15	02-Jul-15	195																	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D10-D09 Northern Side	
1061-1065.6.1	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D12 Southern Side	14	13-May-15	28-May-15	195																	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D12 Southern Side	
1061-1065.6.2	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D10 Southern Side	14	29-May-15	13-Jun-15	195																	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D10 Southern Side	
1061-1065.6.3	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D10-D09 Southern Side	14	15-Jun-15	02-Jul-15	195																	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D10-D09 Southern Side	
1061-1068	Install & Operate Dewatering System (excl IIB) - Appr. Ramp > Pier D06-D08	14	20-May-15	04-Jun-15	231																	Install & Operate Dewatering System (excl IIB) - Appr. Ramp > Pier D06-D08	
1061-1068.1	Install & Operate Dewatering System (excl IIB) - Appr. Ramp > Pier D08-D10	14	05-Jun-15	22-Jun-15	231																	Install & Operate Dewatering System (excl IIB) - Appr. Ramp > Pier D08-D10	
10.6.2 - Approach Ramp (Within Portion IIB)																							
Bored Piles																							
1061-1045	Pre-bored H-piles BN01 - A	8	29-May-15	06-Jun-15	439																	Pre-bored H-piles BN01 - A	
1061-1046	Pre-bored H-piles BN01 - B	8	08-Jun-15	16-Jun-15	439																	Pre-bored H-piles BN01 - B	
1061-1047	Pre-bored H-piles BN05 - A	8	17-Jun-15	26-Jun-15	439																	Pre-bored H-piles BN05 - A	
10.7 - Section X - Miscellaneous Works																							
10.7.1 - TTM Stages																							
1071-1025	TTM Stage 2B - TMLG / TD / Police Consultation and Endorsement	7	29-Sep-14 A	27-Mar-15	0																	TTM Stage 2B - TMLG / TD / Police Consultation and Endorsement	

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 March to 19 June 2015)

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2015															
						March				April				May				June			
						08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21
1071-1030	TTM Stage 2B - TTM Enabling Works	2	28-Mar-15	29-Mar-15	0																
1071-1040	TTM Stage 2B - Divert 3 Lanes to E/B Bridge through 'Bridge From Pier17 to Pier D1'	0		29-Mar-15	0																
1071-1041	TTM Stage 2B1 - TMLG / TD / Police Consultation and Endorsement	29	20-Mar-15	17-Apr-15	0																
1071-1042	TTM Stage 2B1 - TTM Enabling Works	2	18-Apr-15	19-Apr-15	0																
1071-1043	TTM Stage 2B1 - Use Existing E/B Lane to Divert 4 W/B Lane	0		19-Apr-15	0																
1071-1045	TTM Stage 2C - TMLG / TD / Police Consultation and Endorsement	71	24-Mar-15	02-Jun-15	0																
1071-1046	TTM Stage 2C - TTM Enabling Works	2	01-Jun-15	02-Jun-15	0																
1071-1047	TTM Stage 2C - Hing Fat Slip Road Divert 4 Lanes to New E/B Bridge through 'TA2' to Rel	0		02-Jun-15	0																

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Contract HY/2009/19

Three Months Rolling Programme (20 March to 19 June 2015)

WP13-0

Layout: CWB - Working Layout for DWP Rev M

Date Printed 26-Sep-14 11

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015					2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
HY/2009/15 - Works Programme Rev. M (DD:20-Sep-12)														
Works in East Ventilation Adit - Based on Alternative Method														
Reinstatement of Breakwater														
S3_54840	Reinstatement works -west side	7d/wk-1	60d	21-Feb-14 08 A	30-Sep-14 18	-85d		Reinstatement works -west side						
S3_60085	Reinstatement works east side	7d/wk-1	60d	31-May-14 08 A	30-Sep-14 18	-85d		Reinstatement works east side						
S3_54845	Completion of Section 3 (KD8) in EVA Area (Alternative Method)	7d/wk-2	0d		30-Sep-14 18	-86d		Completion of Section 3 (KD8) in EVA Area (Alternative Method)						
Works in TS1/TS2 - OHVD and Cable Trough/Maintenance Walkway														
TS2 - OHVD and Cable Trough/Maintenance Walkway														
OHVD Slab and Cable Trough Construction														
S3_6210	TS2 - OHVD/ Cable trough	7d/wk-1	40d	20-May-14 08 A	30-Sep-14 18	-85d		TS2 - OHVD/ Cable trough						
S3_6212	Completion of Section 3 - TS1/TS2 Area (below -6mpd) KD8)	7d/wk-2	0d		30-Sep-14 18	-86d		Completion of Section 3 - TS1/TS2 Area (below -6mpd) KD8)						
Works in TS4/ME4 Area (Portion 14A, 14B, 15, 23)														
TS4/ME4 - Removal of Temporary Reclamation														
Remaining Works at TZ6														
Stage 4 - Seawall and Reclamation at TZ6														
A-2010	Installation of seawall blocks (Qty: 245 nos.)	7d/wk-2	6d	15-Sep-14 08 A	26-Sep-14 18	-332d		Installation of seawall blocks (Qty: 245 nos.)						
A-2020	Soil Backfilling up to -2.45mPD (Qty:3,000 cu.m.)	7d/wk-2	2d	25-Sep-14 08	26-Sep-14 18	-332d		Soil Backfilling up to -2.45mPD (Qty:3,000 cu.m.)						
A-2030	Utilities installation for Mined Tunnel	7d/wk-2	1d	27-Sep-14 08	27-Sep-14 18	-332d		Utilities installation for Mined Tunnel						
A-2040	Soil backfilling up to ground level (Qty:2,000 cu.m.)	7d/wk-2	2d	28-Sep-14 08	29-Sep-14 18	-332d		Soil backfilling up to ground level (Qty:2,000 cu.m.)						
A-2050	Site clearance	7d/wk-2	1d	30-Sep-14 08	30-Sep-14 18	-305d		Site clearance						
A-2060	Handover to MTR	7d/wk-2	0d		30-Sep-14 18	-305d		Handover to MTR						
Removal of Temporary Reclamation at TS4/ME4														
Stage 5 (Zones A, D & F - TS4-D33 to D-26, SCL2 & ME4-D19 to D13)														
A-3000	D-Wall horizontal cutting (Qty: 62 pcs.)	7d/wk-2	21d	29-Aug-14 08 A	23-Sep-14 18	-340d		D-Wall horizontal cutting (Qty: 62 pcs.)						
Stage 6 (Zone C - P4, ME4-D12 to ME4-D18 & P3)														
A-3011	Marine removal of temporary reclamation and seawall blocks (Zones C)	7d/wk-2	21d	31-Aug-14 08 A	02-Oct-14 18	-353d		Marine removal of temporary reclamation and seawall blocks (Zones C)						
A-3030	D-Wall vertical cutting (Qty: 15 pcs.)	7d/wk-2	4d	03-Oct-14 08	06-Oct-14 18	-353d		D-Wall vertical cutting (Qty: 15 pcs.)						
A-3040	D-Wall horizontal cutting (Qty: 20 pcs.)	7d/wk-2	5d	06-Oct-14 08	10-Oct-14 18	-352d		D-Wall horizontal cutting (Qty: 20 pcs.)						

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

1 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float												
							2015			2016								
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
Stage 7 (Zones C & E - ME4-D06 to D01, SCL1 & TS4-D25)																		
A-4000	Marine removal of temporary reclamation and seawall blocks (Zones C & E)	7d/wk-2	18d	06-Sep-14 08 A	06-Oct-14 18	-353d	<div></div>	Marine removal of temporary reclamation and seawall blocks (Zones C & E)										
A-3090	Hole coring (Qty: 44 nos)	7d/wk-2	9d	20-Sep-14 08*	28-Sep-14 18	-346d	<div></div>	Hole coring (Qty: 44 nos)										
A-4010	D-Wall vertical cutting (Qty: 27pcs.)	7d/wk-2	7d	07-Oct-14 08	13-Oct-14 18	-353d	<div></div>	D-Wall vertical cutting (Qty: 27pcs.)										
A-4020	D-Wall horizontal cutting (Qty: 37 pcs.)	7d/wk-2	10d	11-Oct-14 08	20-Oct-14 18	-353d	<div></div>	D-Wall horizontal cutting (Qty: 37 pcs.)										
Stage 9 (Zone I - TS4-D01 to TS4-D08)																		
A-3050	Remaining removal of temporary reclamation (Zone I)	7d/wk-2	28d	29-Aug-14 08 A	01-Oct-14 18	-342d	<div></div>	Remaining removal of temporary reclamation (Zone I)										
A-3060	Hole coring (Qty: 25 nos)	7d/wk-2	5d	02-Oct-14 08	06-Oct-14 18	-342d	<div></div>	Hole coring (Qty: 25 nos)										
A-3070	D-Wall vertical cutting (Qty: 14 pcs.)	7d/wk-2	3d	07-Oct-14 08	09-Oct-14 18	-342d	<div></div>	D-Wall vertical cutting (Qty: 14 pcs.)										
A-3080	D-Wall horizontal cutting (Qty: 24 pcs.)	7d/wk-2	5d	21-Oct-14 08	25-Oct-14 18	-353d	<div></div>	D-Wall horizontal cutting (Qty: 24 pcs.)										
Stage 8 (Zones G & K - TS4-D24 to TS4-D15)																		
A-4040	Relocation of RHKYC floating pontoon	7d/wk-2	5d	22-Sep-14 08*	26-Sep-14 18	-338d	<div></div>	Relocation of RHKYC floating pontoon										
A-4050	Hole coring (Qty: 27 nos)	7d/wk-2	6d	29-Sep-14 08	04-Oct-14 18	-346d	<div></div>	Hole coring (Qty: 27 nos)										
A-4060	Marine removal of temporary reclamation and seawall blocks (Zone G & K)	7d/wk-2	14d	11-Oct-14 08	24-Oct-14 18	-352d	<div></div>	Marine removal of temporary reclamation and seawall blocks (Zone G & K)										
A-4070	D-Wall vertical cutting (Qty: 18pcs.)	7d/wk-2	4d	25-Oct-14 08	28-Oct-14 18	-352d	<div></div>	D-Wall vertical cutting (Qty: 18pcs.)										
A-4080	D-Wall horizontal cutting (Qty: 25 pcs.)	7d/wk-2	7d	26-Oct-14 08	01-Nov-14 18	-352d	<div></div>	D-Wall horizontal cutting (Qty: 25 pcs.)										
Stage 10 (Zone J - TS4-D09 to TS4-D14)																		
A-4090	Land removal of temporary reclamation (Zone J)	7d/wk-2	10d	07-Oct-14 08	16-Oct-14 18	-344d	<div></div>	Land removal of temporary reclamation (Zone J)										
A-5000	Hole coring (Qty: 32 nos)	7d/wk-2	7d	17-Oct-14 08	23-Oct-14 18	-340d	<div></div>	Hole coring (Qty: 32 nos)										
A-5010	Marine removal of temporary reclamation (Zone J)	7d/wk-2	7d	26-Oct-14 08	01-Nov-14 18	-353d	<div></div>	Marine removal of temporary reclamation (Zone J)										
A-5020	D-Wall vertical cutting (Qty: 20 pcs.)	7d/wk-2	5d	02-Nov-14 08	06-Nov-14 18	-353d	<div></div>	D-Wall vertical cutting (Qty: 20 pcs.)										
A-5030	D-Wall horizontal cutting (Qty: 26 pcs.)	7d/wk-2	7d	04-Nov-14 08	10-Nov-14 18*	-353d	<div></div>	D-Wall horizontal cutting (Qty: 26 pcs.)										
Stage 13 - Phase 3 Mooring																		
A-5050	Final trimming of sea bed level	7d/wk-2	4d	02-Nov-14 08	05-Nov-14 18	-347d	<div></div>	Final trimming of sea bed level										
A-5060	Phase 3 Mooring	7d/wk-2	6d	06-Nov-14 08	11-Nov-14 18	-347d	<div></div>	Phase 3 Mooring										
A-5040	Reinstatement of existing seawall (Zones I & J)	7d/wk-2	7d	11-Nov-14 08	17-Nov-14 18	-353d	<div></div>	Reinstatement of existing seawall (Zones I & J)										
Stage 12 - Re-provisioning of Jetty																		
S6_5258	Provision of Mobile Crane (until permanent re-provision of Jetty is completed)	7d/wk-1	160d	20-Feb-14 08 A	30-Dec-14 18	-335d	<div></div>	Provision of Mobile Crane (until permanent re-provision of Jetty is completed)										
A-6010	BA8 submission and consent for commencement of superstructure	7d/wk-2	28d	20-Sep-14 08 A	16-Oct-14 18	-336d	<div></div>	BA8 submission and consent for commencement of superstructure										

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

2 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015					2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A-8012	Submission of performance report	7d/wk-2	1d	25-Oct-14 08*	25-Oct-14 18	-286d								
A-8020	Erection of working platform for jetty beams and reinstate the floating portoon	7d/wk-2	10d	02-Nov-14 08	11-Nov-14 18	-352d								
A-8040	BA10 submission for authorized signatory and subcontractor	7d/wk-2	1d	12-Nov-14 08	12-Nov-14 18	-304d								
A-8030	Jetty beams construction	7d/wk-2	14d	12-Nov-14 08	25-Nov-14 18	-352d								
A-8052	Construction of floating pontoon	7d/wk-2	14d	26-Nov-14 08	09-Dec-14 18	-331d								
A-8050	BA13 submission + 14-day cube test results	7d/wk-2	28d	26-Nov-14 08	23-Dec-14 18	-352d								
A-8060	E&M and accessories installation	7d/wk-2	7d	24-Dec-14 08	30-Dec-14 18	-352d								
A-8070	Handover to RHKYC	7d/wk-2	1d	31-Dec-14 08	31-Dec-14 18	-352d								
Stage 11 - Construction of TZ4														
A-8080	South side - laying rockfill and levelling stone (Qty: 1,550 cu.m)	7d/wk-2	12d	24-Sep-14 08	05-Oct-14 18	-339d								
A-8090	South side - install seawall blocks (Qty: 255 nos.)	7d/wk-2	6d	06-Oct-14 08	11-Oct-14 18	-339d								
A-7000	South side - general fill (Qty: 2,000 cu.m.)	7d/wk-2	2d	12-Oct-14 08	13-Oct-14 18	-339d								
A-7010	North side - laying rockfill and levelling stone (Qty: 1,550 cu.m)	7d/wk-2	12d	21-Oct-14 08	01-Nov-14 18	-346d								
A-7020	North side - install seawall blocks (Qty: 255 nos.)	7d/wk-2	6d	02-Nov-14 08	07-Nov-14 18	-346d								
A-7030	North side - general fill (Qty:2,000 cu.m.)	7d/wk-2	2d	08-Nov-14 08	09-Nov-14 18	-346d								
A-7040	Handover to contract TS3/SR8	7d/wk-2	1d	10-Nov-14 08	10-Nov-14 18*	-346d								
TS4/ME4, Removal of Temporary Reclamation														
S26875	Completion of Section 2 (With ME4 option) (KD7)	7d/wk-2	0d		17-Nov-14 18	-353d								
S26890	Completion of Section 7B (ME4) (KD13)	7d/wk-2	0d		17-Nov-14 18	-353d								
TS4 - OHVD / Cable Trough														
S5_6185	TS4 (incl. TS4+) - OHVD Slab - Area C (access through temp. opening at TZ4)	7d/wk-1	36d	02-Jan-15 08*	06-Feb-15 18	195d								
S5_6190	TS4 (incl. TS4+) - Cable Trough (access through temp. opening at TZ4)	7d/wk-1	60d	07-Feb-15 08*	14-Apr-15 18	195d								
S5_59850	Completion of Section 5 - TS4/ME4 Area (KD10), below -20mPD	7d/wk-2	0d		02-Nov-15 18*	0d								
Works in TPCWAE Area (Portion 20A, 20B)														
Removal of Temporary Reclamation														
Removal of Temporary Reclamation & Form TZ5														
S87670	Remove general fill /sea wall block	7d/wk-1	24d	20-May-14 08 A	08-Oct-14 18	-296d								
S87675	Diaphragm wall saw cutting (1st D Wall cut on 23 Jun 2014)	7d/wk-1	31d	03-Sep-14 08 A	16-Oct-14 18	-306d								
S87755	Form TZ5	7d/wk-1	18d	25-Sep-14 08	14-Oct-14 18	-304d								

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

3 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015									2016																							
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3																									
S67685	Achievement of KD5	7d/wk-2	0d		16-Oct-14 18	-323d		◆ Achievement of KD5																															
S67687	Complete Reinstatement of Vertical Seawall (near PRE Office)	7d/wk-2	0d		27-Oct-14 18	-322d		◆ Complete Reinstatement of Vertical Seawall (near PRE Office)																															
Reinstate Mucking Out Access Shaft "C"																																							
S67240	Start reinstatement works (after completion of TPCWAW OHVD works)	6d/wk	0d	26-Mar-16 08		-102d										◆ Start reinstatement works (after c																							
S67225	Cast slab opening at top of CCT West bound (access shaft)	6d/wk	18d	28-Mar-16 08	16-Apr-16 18	-102d										■ Cast slab opening at top of																							
S67230	Removal of vertical shaft and backfilling	6d/wk	48d	11-Apr-16 08	04-Jun-16 18	-102d										■ Removal of vertical																							
S67235	Reinstatement of pavement	6d/wk	12d	30-May-16 08	11-Jun-16 18	-102d										■ Reinstatement of																							
TPCWAE - OHVD / Cable Trough																																							
S5_7405	TPCWAE - Cable Trough (access through temp. opening at TZ5 & Portion 19)	6d/wk	48d	04-Sep-15 08	02-Nov-15 18	0d										■ TPCWAE - Cable Trough (access through temp. opening at T																							
S5_7400	TPCWAE - OHVD Slab AT Area A (access through temp. opening at TZ5 & Portion 19)	6d/wk	48d	04-Sep-15 08	02-Nov-15 18	0d										■ TPCWAE - OHVD Slab AT Area A (access through temp. open																							
S5_59840	Completion of Section 5 - TPCWAE Area (KD10), below -20mPD	7d/wk-2	0d		02-Nov-15 18*	0d										◆ Completion of Section 5 - TPCWAE Area (KD10), below -20m																							
Works in TPCWAW Area																																							
TPCWAW - Temporary Reclamation																																							
Temporary Reclamation -																																							
S6_9440	TPCWAW - place levelling stone and tamping, South side	7d/wk-1	6d	15-Oct-14 08	20-Oct-14 18	-122d		■ TPCWAW - place levelling stone and tamping, South side																															
S6_9450	TPCWAW - place seawall block to +4 at South side (Qty: 569 nos. @ 50 nos/day)	7d/wk-1	12d	21-Oct-14 08	01-Nov-14 18	-122d		■ TPCWAW - place seawall block to +4 at South side (Qty: 569 nos. @ 50 nos/day)																															
S6_9465	TPCWAW - place levelling stone and tamping, North side	7d/wk-1	6d	02-Nov-14 08	07-Nov-14 18	-122d		■ TPCWAW - place levelling stone and tamping, North side																															
S6_9470	TPCWAW - place seawall blocks to +4 North side (Qty: 672 nos @ 50 nos/day)	7d/wk-1	14d	08-Nov-14 08	21-Nov-14 18	-122d		■ TPCWAW - place seawall blocks to +4 North side (Qty: 672 nos @ 50 nos/day)																															
S6_9495	TPCWAW - General fill to +2 within the seawall	7d/wk-1	17d	15-Nov-14 08	01-Dec-14 18	-122d		■ TPCWAW - General fill to +2 within the seawall																															
S6_9490	TPCWAW - place seawall blocks to +4 at the temporary opening	7d/wk-1	7d	02-Dec-14 08	08-Dec-14 18	-122d		■ TPCWAW - place seawall blocks to +4 at the temporary opening																															
S6_9475	TPCWAW - Remaining General fill to +4 within the seawall	7d/wk-1	10d	09-Dec-14 08	18-Dec-14 18	-122d		■ TPCWAW - Remaining General fill to +4 within the seawall																															
TPCWAW - Diaphragm Wall																																							
Diaphragm Wall																																							
S6_9385	Site investigation	7d/wk-1	49d	01-Dec-14 08	21-Jan-15 18	-113d		■ Site investigation																															
S6_8960	Install guide wall	7d/wk-1	40d	17-Dec-14 08	28-Jan-15 18	-120d		■ Install guide wall																															
S6_8955	Curtain grout along proposed diaphragm wall	7d/wk-1	40d	19-Dec-14 08	30-Jan-15 18	-122d		■ Curtain grout along proposed diaphragm wall																															
S6_9382	Set up bentonite silo/plants and equipments	7d/wk-1	30d	19-Dec-14 08	20-Jan-15 18	-112d		■ Set up bentonite silo/plants and equipments																															
S6_9345	Diaphragm wall construction (34 panels @ 3 panels/ week)	7d/wk-1	68d	30-Jan-15 08	14-Apr-15 18	-141d		■ Diaphragm wall construction (34 panels @ 3 panels/ week)																															
S6_9350	Install shear pins on diaphragm wall	7d/wk-1	40d	14-Mar-15 08	26-Apr-15 18	-133d		■ Install shear pins on diaphragm wall																															
<div><div><div>Summary Bar</div><div>Actual Level of Effort</div><div>Actual Work</div><div>Remaining Work</div><div>Critical Remaining Work</div><div>◆ Milestone</div></div></div>							<div>4 of 18</div> <div>China State Construction Engineering (Hong Kong) Ltd</div> <div>Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)</div> <div>WORKS PROGRAMME REV. M</div>							<div>Prepared by William Caluza</div> <table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>26-Sep...</td><td>1st submission</td><td></td><td></td></tr><tr><td></td><td></td><td></td><td></td></tr><tr><td></td><td></td><td></td><td></td></tr><tr><td></td><td></td><td></td><td></td></tr></table>				Date	Revision	Checked	Approved	26-Sep...	1st submission															<div><div>CSECE</div><div>中國建築工程(香港)有限公司</div><div>CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.</div></div>	
Date	Revision	Checked	Approved																																				
26-Sep...	1st submission																																						

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float									
							2015			2016					
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
S6_9355	Install king posts	7d/wk-1	40d	14-Mar-15 08	26-Apr-15 18	-133d			Install king posts						
S6_8970	Diaphragm Wall Pile test	7d/wk-1	40d	20-Mar-15 08	03-May-15 18	-129d			Diaphragm Wall Pile test						
S6_9375	Carry out contact/fissure grouting	7d/wk-1	29d	21-Mar-15 08	22-Apr-15 18	-141d			Carry out contact/fissure grouting						
TPCWAW- ELS Works															
ELS Works															
S6_9360	Install dewatering wells and piezometers	7d/wk-1	20d	30-Mar-15 08	22-Apr-15 18	-141d			Install dewatering wells and piezometers						
S6_9365	Install inclinometers inside D-wall	7d/wk-1	20d	15-Apr-15 08	05-May-15 18	-141d			Install inclinometers inside D-wall						
S6_8975	Carry out pumping tests	7d/wk-1	12d	23-Apr-15 08	05-May-15 18	-141d			Carry out pumping tests						
S6_8980	1st Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	06-May-15 08	15-May-15 18	-141d			1st Layer - D Wall conc over break if any & Soft Excavation						
S6_9260	Submit pumping test report	7d/wk-1	1d	06-May-15 08	06-May-15 18	-137d			Submit pumping test report						
S6_8985	1st Layer - install lateral support	7d/wk-1	10d	16-May-15 08	26-May-15 18	-141d			1st Layer - install lateral support						
S6_8990	Install vibrating wire strain gauge	7d/wk-1	10d	16-May-15 08	26-May-15 18	-141d			Install vibrating wire strain gauge						
S6_8995	2nd Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	18-May-15 08	28-May-15 18	-141d			2nd Layer - D Wall conc over break if any & Soft Excavation						
S6_9000	2nd Layer - install lateral support	7d/wk-1	10d	29-May-15 08	07-Jun-15 18	-141d			2nd Layer - install lateral support						
S6_9005	3rd Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	31-May-15 08	09-Jun-15 18	-141d			3rd Layer - D Wall conc over break if any & Soft Excavation						
S6_9010	3rd Layer - install lateral support	7d/wk-1	10d	10-Jun-15 08	19-Jun-15 18	-141d			3rd Layer - install lateral support						
S6_9015	4th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	12-Jun-15 08	22-Jun-15 18	-141d			4th Layer - D Wall conc over break if any & Soft Excavation						
S6_9020	4th Layer - install lateral support	7d/wk-1	10d	23-Jun-15 08	03-Jul-15 18	-141d			4th Layer - install lateral support						
S6_9025	5th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	25-Jun-15 08	05-Jul-15 18	-141d			5th Layer - D Wall conc over break if any & Soft Excavation						
S6_9030	5th Layer - install lateral support	7d/wk-1	10d	27-Jun-15 08	07-Jul-15 18	-141d			5th Layer - install lateral support						
S6_9035	6th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	08-Jul-15 08	17-Jul-15 18	-141d			6th Layer - D Wall conc over break if any & Soft Excavation						
S6_9040	6th Layer - install lateral support	7d/wk-1	10d	18-Jul-15 08	27-Jul-15 18	-69d			6th Layer - install lateral support						
TPCWAW - ROCK EXCAVATION															
S6_6180	Rock excavation to formation	7d/wk-1	112d	18-Jul-15 08	09-Nov-15 18	-141d			Rock excavation to formation						
S6_9370	Install tie back anchor to D- Walls (area on west side, near Portion 11)	7d/wk-1	25d	20-Jul-15 08	13-Aug-15 18	-69d			Install tie back anchor to D- Walls (area on west side, near Portion 11)						
S6_9415	Install tie back anchor to D- Walls (east area)	7d/wk-1	20d	20-Jul-15 08	08-Aug-15 18	-69d			Install tie back anchor to D- Walls (east area)						
S6_9055	Provide Access to WDII Contractor for demolition of bulkhead at Portion 11	7d/wk-2	0d		10-Nov-15 18	-133d			Provide Access to WDII Contractor for demolition of bulkhead						
TPCWAW- CCT RC Structure															
TPCWAW - CCT / OHVD															

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015								2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
S6_9070	TPCWAW Construct tunnel base slab	7d/wk-1	50d	23-Oct-15 08	11-Dec-15 18	-141d									TPCWAW Construct tunnel base slab			
S6_9075	TPCWAW Construct tunnel wall + OHVD + roof slab	7d/wk-1	80d	13-Nov-15 08	02-Feb-16 18	-141d									TPCWAW Construct tunnel wall + OHVD +			
S6_9077	TPCWAW - external waterproofing on top of completed CCT box (incl. screeding)	7d/wk-1	26d	03-Feb-16 08	28-Feb-16 18	-120d									TPCWAW - external waterproofing on			
S6_9076	TPCWAW King post load transfer	7d/wk-1	26d	03-Feb-16 08	28-Feb-16 18	-120d									TPCWAW King post load transfer			
TPCWAW - Removal of Temporary Reclamation																		
Removal of Temporary Reclamation																		
S6_9140	Backfilling/Removal of ELS/ Reinstatement of sea wall at Portion 11 (concurrent activities)	7d/wk-1	30d	17-Feb-16 08	17-Mar-16 18	-120d									Backfilling/Removal of ELS/ Reinsta			
S6_9105	Remove general fill/ seawall block (concurrent activities)	7d/wk-1	25d	06-Mar-16 08	30-Mar-16 18	-120d									Remove general fill/ seawall bloc			
S6_9120	Saw cut diaphragm wall	7d/wk-1	63d	21-Mar-16 08	23-May-16 18	-120d									Saw cut diaphragm w			
S6_7550	Completion of Section 6- (KD11), above - 20mPD	7d/wk-2	0d		23-May-16 18	-121d									Completion of Section			
TPCWAW -Cable Trough/ Maintenance Walkway																		
S6_9085	TPCWAW - Cable Trough (access through temp. opening at Portion 19)	7d/wk-2	24d	02-Mar-16 08	25-Mar-16 18	-144d									TPCWAW - Cable Trough (access			
S6_9135	Completion of Section 5 - TPCWAW Area (KD10), below -20mPD	7d/wk-2	0d		25-Mar-16 18	-144d									Completion of Section 5 - TPCWA			
Works in Wan Chai PCWA (Portion 11)																		
Initial Works & Utilities Works																		
S4_2810	Installation of Hoarding	7d/wk-1	24d	05-May-14 08 A	17-Oct-14 18	-58d									Installation of Hoarding			
S4_2720	Remove existing rock mound	7d/wk-1	24d	21-Oct-14 08	13-Nov-14 18	-61d									Remove existing rock mound			
S4_2750	Carry out Site Investigation for BW1/BW2	7d/wk-1	12d	21-Oct-14 08	01-Nov-14 18	-61d									Carry out Site Investigation for BW1/BW2			
S4_2755	BW1/BW2 Engineers confirmation of provisional Barrettes	7d/wk-1	0d		07-Nov-14 18	-61d									BW1/BW2 Engineers confirmation of provisional Barrettes			
Allow Access to WDII																		
S4_2785	Complete Section 4 - Portion 11 (KD9)	7d/wk-2	0d		10-Nov-15 18	-132d									Complete Section 4 - Portion 11 (KD9)			
S4_2775	Return Portion 11 to WDII	7d/wk-1	0d		10-Nov-15 18	-129d									Return Portion 11 to WDII			
Works for Mined Tunnel (Portion 16, 17, 18)																		
SR8 (Tunnel Excavation + Lining)																		
From West (TPCWAE)																		
Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																		
A8676	SR8 Heading Excavation From West, CH 4095- 4107 = 8m @2d/m	7d/wk-1a	16d	03-Sep-14 08 A	28-Sep-14 18	164d									SR8 Heading Excavation From West, CH 4095- 4107 = 8m @2d/m			
Bench Excavation (1.5d-2d/m, 20m separation with heading)																		
A8700	SR8 Bench Excavation From West, CH 4055- 4065 = 10m	7d/wk-1a	20d	08-Sep-14 08 A	24-Sep-14 18	148d									SR8 Bench Excavation From West, CH 4055- 4065 = 10m			
6 of 18							Prepared by William Caluza				Date		Revision		Checked		Approved	
China State Construction Engineering (Hong Kong) Ltd											26-Sep...		1st submission					
Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)																		
WORKS PROGRAMME REV. M																		
Summary Bar																		
Actual Level of Effort																		
Actual Work																		
Remaining Work																		
Critical Remaining Work																		
Milestone																		

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A8705	SR8 Bench Excavation From West, CH 4065- 4075 = 10m	7d/wk-1a	20d	25-Sep-14 08	15-Oct-14 18	148d								
A8685	SR8 Bench Excavation From West, CH 4075- 4085 = 10m	7d/wk-1a	20d	16-Oct-14 08	04-Nov-14 18	148d								
A8680	SR8 Bench Excavation From West, CH 4085- 4095 = 10m	7d/wk-1a	20d	05-Nov-14 08	24-Nov-14 18	148d								
A8725	SR8 Bench Excavation From West, CH 4095- 4100 = 5m	7d/wk-1a	10d	25-Nov-14 08	04-Dec-14 18	148d								
From East (TS4)														
Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)														
A8495	SR8 Heading Excavation From East CH 4115- 4107 = 8m @2d/m	7d/wk-1a	16d	15-Sep-14 08 A	28-Sep-14 18	10d								
Bench Excavation (1.5d/m, 20m separation with heading)														
A8455	SR8 Bench Excavation From East, CH 4147.5- 4135 = 12.5m	7d/wk-1a	19d	20-Sep-14 08	09-Oct-14 18	0d								
A8470	SR8 Bench Excavation From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	10-Oct-14 08	24-Oct-14 18	0d								
A8460	SR8 Bench Excavation From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	25-Oct-14 08	08-Nov-14 18	0d								
A8465	SR8 Bench Excavation From East, CH 4115- 4100 = 15m	7d/wk-1a	23d	09-Nov-14 08	01-Dec-14 18	0d								
Tunnel Lining Works														
From West - Base Slab (10m/bay, 10m separation with benching excavation)														
A8525	SR8, From West, CH 4015 - 4025 = 10m/bay, base slab	7d/wk-1a	10d	15-Sep-14 08 A	04-Oct-14 18	137d								
A8530	SR8, From West,CH 4025 - 4035 = 10m/bay, base slab	7d/wk-1a	10d	05-Oct-14 08	14-Oct-14 18	163d								
A8535	SR8, From West,CH 4035 - 4045 = 10m/bay, base slab	7d/wk-1a	8d	15-Oct-14 08	22-Oct-14 18	165d								
A8540	SR8, From West, CH 4045 - 4055 = 10m/bay, base slab	7d/wk-1a	8d	23-Oct-14 08	30-Oct-14 18	165d								
A8545	SR8, From West, CH 4055 - 4065 = 10m/bay, base slab	7d/wk-1a	8d	05-Nov-14 08	12-Nov-14 18	160d								
A8550	SR8, From West, CH 4065 - 4075 = 10m/bay, base slab	7d/wk-1a	8d	25-Nov-14 08	02-Dec-14 18	148d								
A8555	SR8, From West, CH 4075 - 4085 = 10m/bay, base slab	7d/wk-1a	8d	05-Dec-14 08	12-Dec-14 18	148d								
A8560	SR8, From West, CH 4085 - 4095 = 10m/bay, base slab	7d/wk-1a	8d	13-Dec-14 08	20-Dec-14 18	150d								
A8561	SR8, From West, CH 4095 - 4105 = 10m/bay, base slab	7d/wk-1a	8d	21-Dec-14 08	29-Dec-14 18	152d								
A8562	SR8, From West, CH 4105 - 4115 = 10m/bay, base slab	7d/wk-1a	8d	30-Dec-14 08	07-Jan-15 18	154d								
From West - Lining (5m/bay, 10m separation with base slab)														
A8575	SR8, From West, CH 3995 - 4000 = 1bay, lining	7d/wk-1a	9d	20-Sep-14 08	28-Sep-14 18	0d								
A8580	SR8, From West, CH 4000 - 4005 = 1bay, lining	7d/wk-1a	9d	05-Oct-14 08	13-Oct-14 18	137d								
A8585	SR8, From West, CH 4005 - 4010 = 1bay, lining	7d/wk-1a	9d	14-Oct-14 08	22-Oct-14 18	137d								
A8590	SR8, From West, CH 4010 - 4015 = 1bay, lining	7d/wk-1a	9d	23-Oct-14 08	31-Oct-14 18	137d								

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

7 of 18


China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015					2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A8595	SR8, From West, CH 4015 - 4020 = 1bay, lining	7d/wk-1a	9d	01-Nov-14 08	09-Nov-14 18	137d	■ SR8, From West, CH 4015 - 4020 = 1bay, lining							
A8600	SR8, From West, CH 4020 - 4025 = 1bay, lining	7d/wk-1a	9d	10-Nov-14 08	18-Nov-14 18	137d	■ SR8, From West, CH 4020 - 4025 = 1bay, lining							
A8605	SR8, From West, CH 4025 - 4030 = 1bay, lining	7d/wk-1a	5d	19-Nov-14 08	23-Nov-14 18	137d	■ SR8, From West, CH 4025 - 4030 = 1bay, lining							
A8610	SR8, From West, CH 4030 - 4035 = 1bay, lining	7d/wk-1a	5d	24-Nov-14 08	28-Nov-14 18	137d	■ SR8, From West, CH 4030 - 4035 = 1bay, lining							
A8615	SR8, From West, CH 4035 - 4040 = 1bay, lining	7d/wk-1a	5d	29-Nov-14 08	03-Dec-14 18	137d	■ SR8, From West, CH 4035 - 4040 = 1bay, lining							
A8620	SR8, From West, CH 4040 - 4045 = 1bay, lining	7d/wk-1a	5d	04-Dec-14 08	08-Dec-14 18	137d	■ SR8, From West, CH 4040 - 4045 = 1bay, lining							
A8625	SR8, From West, CH 4045 - 4050 = 1bay, lining	7d/wk-1a	5d	09-Dec-14 08	13-Dec-14 18	137d	■ SR8, From West, CH 4045 - 4050 = 1bay, lining							
A8630	SR8, From West, CH 4050 - 4055 = 1bay, lining	7d/wk-1a	5d	14-Dec-14 08	18-Dec-14 18	137d	■ SR8, From West, CH 4050 - 4055 = 1bay, lining							
A8635	SR8, From West, CH 4055 - 4060 = 1bay, lining	7d/wk-1a	5d	19-Dec-14 08	23-Dec-14 18	137d	■ SR8, From West, CH 4055 - 4060 = 1bay, lining							
A8640	SR8, From West, CH 4060 - 4065 = 1bay, lining	7d/wk-1a	5d	24-Dec-14 08	29-Dec-14 18	137d	■ SR8, From West, CH 4060 - 4065 = 1bay, lining							
A8645	SR8, From West, CH 4065 - 4070 = 1bay, lining	7d/wk-1a	5d	30-Dec-14 08	04-Jan-15 18	137d	■ SR8, From West, CH 4065 - 4070 = 1bay, lining							
A8647	SR8, From West, CH 4070 - 4075 = 1bay, lining	7d/wk-1a	5d	05-Jan-15 08	09-Jan-15 18	137d	■ SR8, From West, CH 4070 - 4075 = 1bay, lining							
A8648	SR8, From West, CH 4075 - 4080 = 1bay, lining	7d/wk-1a	5d	10-Jan-15 08	14-Jan-15 18	137d	■ SR8, From West, CH 4075 - 4080 = 1bay, lining							
A8649	SR8, From West, CH 4080 - 4085 = 1bay, lining	7d/wk-1a	5d	15-Jan-15 08	19-Jan-15 18	137d	■ SR8, From West, CH 4080 - 4085 = 1bay, lining							
A8651	SR8, From West, CH 4085 - 4090 = 1bay, lining	7d/wk-1a	5d	20-Jan-15 08	24-Jan-15 18	137d	■ SR8, From West, CH 4085 - 4090 = 1bay, lining							
A8652	SR8, From West, CH 4090 - 4095 = 1bay, lining	7d/wk-1a	5d	25-Jan-15 08	29-Jan-15 18	137d	■ SR8, From West, CH 4090 - 4095 = 1bay, lining							
A8653	SR8, From West, CH 4095 - 4100 = 1bay, lining	7d/wk-1a	5d	30-Jan-15 08	03-Feb-15 18	137d	■ SR8, From West, CH 4095 - 4100 = 1bay, lining							
A8654	SR8, From West, CH 4100 - 4105 = 1bay, lining	7d/wk-1a	5d	04-Feb-15 08	08-Feb-15 18	137d	■ SR8, From West, CH 4100 - 4105 = 1bay, lining							
From East - Base Slab (10m/bay, 10m separation with benching excavation)														
A9775	SR8 From East, CH 4149.5 - 4145 = 4.5m, base slab	7d/wk-1a	8d	02-Dec-14 08	09-Dec-14 18	0d	■ SR8 From East, CH 4149.5 - 4145 = 4.5m, base slab							
A9780	SR8 From East, CH 4145 - 4135 = 10m/bay, base slab	7d/wk-1a	8d	10-Dec-14 08	17-Dec-14 18	0d	■ SR8 From East, CH 4145 - 4135 = 10m/bay, base slab							
A9785	SR8 From East, CH 4135 - 4125 = 10m/bay, base slab	7d/wk-1a	8d	18-Dec-14 08	26-Dec-14 18	8d	■ SR8 From East, CH 4135 - 4125 = 10m/bay, base slab							
A9786	SR8 From East, CH 4125 - 4115 = 10m/bay, base slab	7d/wk-1a	8d	27-Dec-14 08	04-Jan-15 18	10d	■ SR8 From East, CH 4125 - 4115 = 10m/bay, base slab							
From East - Lining (5m/bay, 10m separation with base slab)														
A9820	From East, SR8 CH 4149.5 - 4145 = 4.5m, 1 bay, lining	7d/wk-1a	5d	18-Dec-14 08	22-Dec-14 18	0d	■ From East, SR8 CH 4149.5 - 4145 = 4.5m, 1 bay, lining							
A9815	From East, SR8 CH 4145 - 4140 = 1bay, lining	7d/wk-1a	5d	23-Dec-14 08	28-Dec-14 18	6d	■ From East, SR8 CH 4145 - 4140 = 1bay, lining							
A9810	From East, SR8 CH 4140 - 4135 = 1bay, lining	7d/wk-1a	5d	29-Dec-14 08	03-Jan-15 18	6d	■ From East, SR8 CH 4140 - 4135 = 1bay, lining							
A9805	From East, SR8 CH 4135 - 4130 = 1bay, lining	7d/wk-1a	5d	04-Jan-15 08	08-Jan-15 18	6d	■ From East, SR8 CH 4135 - 4130 = 1bay, lining							

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

8 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)


WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2
A9870	From East, SR8 CH 4130 - 4125 = 1bay, lining	7d/wk-1a	5d	09-Jan-15 08	13-Jan-15 18	6d			■ From East, SR8 CH 4130 - 4125 = 1bay, lining				
A9800	From East, SR8 CH 4125 - 4120 = 1bay, lining	7d/wk-1a	5d	14-Jan-15 08	18-Jan-15 18	143d			■ From East, SR8 CH 4125 - 4120 = 1bay, lining				
A9860	From East, SR8 CH 4120 - 4115 = 1bay, lining	7d/wk-1a	5d	19-Jan-15 08	23-Jan-15 18	143d			■ From East, SR8 CH 4120 - 4115 = 1bay, lining				
A9855	From East, SR8 CH 4115 - 4110 = 1bay, lining	7d/wk-1a	5d	24-Jan-15 08	28-Jan-15 18	143d			■ From East, SR8 CH 4115 - 4110 = 1bay, lining				
A9850	From East, SR8 CH 4110 - 4105 = 1bay, lining	7d/wk-1a	5d	29-Jan-15 08	02-Feb-15 18	143d			■ From East, SR8 CH 4110 - 4105 = 1bay, lining				
OHVD(10m/bay) / Utility Trough													
A8570	SR8 Tunnel OHVD and utility trough =, 167= 17 bays @ 10m/bay @ 7d/bay	7d/wk-1a	120d	09-Feb-15 08	13-Jun-15 18	137d			■ SR8 Tunnel OHVD and utility trough = 167= 17 bays @ 10m/bay @ 7d/bay				
EB Outer Tunnel Excavation													
From West (TPCWAE)													
Outer Bench Excavation (1.5d - 2d/m, 20m separation with heading)													
A9550	EB, Outer Bench From West, CH 4035- 4045 = 10m	7d/wk-1a	30d	07-Aug-14 08 A	20-Oct-14 18	135d	■		EB, Outer Bench From West, CH 4035- 4045 = 10m				
A9555	EB, Outer Bench From West, CH 4045- 4055 = 10m (2d/m)	7d/wk-1a	20d	20-Oct-14 08	08-Nov-14 18	135d	■		EB, Outer Bench From West, CH 4045- 4055 = 10m (2d/m)				
A9560	EB, Outer Bench From West, CH 4055- 4065 = 10m (2d/m)	7d/wk-1a	20d	09-Nov-14 08	28-Nov-14 18	135d	■		EB, Outer Bench From West, CH 4055- 4065 = 10m (2d/m)				
A9565	EB, Outer Bench From West, CH 4065- 4075 = 10m (2d/m)	7d/wk-1a	20d	29-Nov-14 08	18-Dec-14 18	135d	■		EB, Outer Bench From West, CH 4065- 4075 = 10m (2d/m)				
A9520	EB, Outer Bench From West, CH 4075- 4085 = 10m (2d/m)	7d/wk-1a	20d	19-Dec-14 08	09-Jan-15 18	135d	■		EB, Outer Bench From West, CH 4075- 4085 = 10m (2d/m)				
A9545	EB, Outer Bench From West, CH 4085- 4095 = 10m 1.5d/m)	7d/wk-1a	15d	10-Jan-15 08	24-Jan-15 18	135d	■		EB, Outer Bench From West, CH 4085- 4095 = 10m 1.5d/m)				
From East (TS4)													
Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)													
A9605	EB, Outer Bench From East, CH 4147.5 - 4145 = 2.5m	7d/wk-1a	30d	20-Oct-14 08*	18-Nov-14 18	120d	■		EB, Outer Bench From East, CH 4147.5 - 4145 = 2.5m				
A9610	EB, Outer Bench From East, CH 4145- 4135 = 10m (2d/m)	7d/wk-1a	20d	19-Nov-14 08	08-Dec-14 18	120d	■		EB, Outer Bench From East, CH 4145- 4135 = 10m (2d/m)				
A9615	EB, Outer Bench From East, CH 4135- 4125 = 10m (2d/m)	7d/wk-1a	20d	09-Dec-14 08	29-Dec-14 18	120d	■		EB, Outer Bench From East, CH 4135- 4125 = 10m (2d/m)				
A9620	EB, Outer Bench From East, CH 4125- 4115 = 10m (2d/m)	7d/wk-1a	20d	30-Dec-14 08	19-Jan-15 18	120d	■		EB, Outer Bench From East, CH 4125- 4115 = 10m (2d/m)				
A9625	EB, Outer Bench From East, CH 4115- 4105 = 10m (2d/m)	7d/wk-1a	20d	20-Jan-15 08	08-Feb-15 18	120d	■		EB, Outer Bench From East, CH 4115- 4105 = 10m (2d/m)				
A9630	EB, Outer Bench From East, CH 4105- 4095 = 10m (1.5d/m)	7d/wk-1a	15d	09-Feb-15 08	26-Feb-15 18	120d	■		EB, Outer Bench From East, CH 4105- 4095 = 10m (1.5d/m)				
EB (Inner Tunnel Excavation + Lining)													
From West (TPCWAE)													
Inner Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)													
A8805	EB,Inner Heading From West, CH 3992- 4005 = 13m @3d/m	7d/wk-1a	39d	29-Sep-14 08	07-Nov-14 18	0d	■		EB,Inner Heading From West, CH 3992- 4005 = 13m @3d/m				
A8815	EB,Inner Heading From West, CH 4005- 4015 = 10m @2d/m	7d/wk-1a	20d	08-Nov-14 08	27-Nov-14 18	0d	■		EB,Inner Heading From West, CH 4005- 4015 = 10m @2d/m				
9 of 18							Prepared by William Caluza						
China State Construction Engineering (Hong Kong) Ltd Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section) WORKS PROGRAMME REV. M							Date	Revision	Checked	Approved	 中國建築工程(香港)有限公司 CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.		
							26-Sep...	1st submission					

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float									
							2015			2016					
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
A8820	EB,Inner Heading From West , CH 4015- 4025 = 10m @2d/m	7d/wk-1a	20d	28-Nov-14 08	17-Dec-14 18	0d		EB,Inner Heading From West , CH 4015- 4025 = 10m @2d/m							
A8780	EB,Inner Heading From West, CH 4025- 4035 = 10m @2d/m	7d/wk-1a	20d	18-Dec-14 08	08-Jan-15 18	0d		EB,Inner Heading From West, CH 4025- 4035 = 10m @2d/m							
A8810	EB,Inner Heading From West , CH 4035- 4045 = 10m @2d/m	7d/wk-1a	20d	09-Jan-15 08	28-Jan-15 18	0d		EB,Inner Heading From West , CH 4035- 4045 = 10m @2d/m							
A8785	EB,Inner Heading From West , CH 4045- 4055 = 10m @2d/m	7d/wk-1a	20d	29-Jan-15 08	17-Feb-15 18	0d		EB,Inner Heading From West , CH 4045- 4055 = 10m @2d/m							
A8790	EB,Inner Heading From West, CH 4055- 4065 = 10m @ 2d/m	7d/wk-1a	20d	18-Feb-15 08	12-Mar-15 18	0d		EB,Inner Heading From West, CH 4055- 4065 = 10m @ 2d/m							
A8795	EB,Inner Heading From West , CH 4065- 4075 = 10m, @ 2d/m	7d/wk-1a	20d	13-Mar-15 08	01-Apr-15 18	0d		EB,Inner Heading From West , CH 4065- 4075 = 10m, @ 2d/m							
A8800	EB,Inner Heading From West, CH 4075- 4085 = 10m @ 2d/m	7d/wk-1a	20d	02-Apr-15 08	22-Apr-15 18	0d		EB,Inner Heading From West, CH 4075- 4085 = 10m @ 2d/m							
A8825	EB,Inner Heading From West, CH 4085- 4095 = 10m @ 2d/m	7d/wk-1a	20d	23-Apr-15 08	13-May-15 18	0d		EB,Inner Heading From West, CH 4085- 4095 = 10m @ 2d/m							
Inner Bench Excavation (1.5-2d/m, 20m separation with heading)															
A8765	EB, Inner Bench From West, CH 3992- 4005 = 13m (2d/m)	7d/wk-1a	26d	08-Nov-14 08	03-Dec-14 18	23d		EB, Inner Bench From West, CH 3992- 4005 = 13m (2d/m)							
A8770	EB, Inner Bench From West,CH 4005- 4015 = 10m	7d/wk-1a	15d	18-Dec-14 08	03-Jan-15 18	9d		EB, Inner Bench From West,CH 4005- 4015 = 10m							
A8775	EB, Inner Bench From West,CH 4015- 4025 = 10m	7d/wk-1a	15d	09-Jan-15 08	23-Jan-15 18	4d		EB, Inner Bench From West,CH 4015- 4025 = 10m							
A8735	EB, Inner Bench From West,CH 4025- 4035 = 10m	7d/wk-1a	15d	29-Jan-15 08	12-Feb-15 18	14d		EB, Inner Bench From West,CH 4025- 4035 = 10m							
A8740	EB, Inner Bench From West,CH 4035- 4045 = 10m	7d/wk-1a	15d	18-Feb-15 08	07-Mar-15 18	11d		EB, Inner Bench From West,CH 4035- 4045 = 10m							
A8745	EB, Inner Bench From West,CH 4045- 4055 = 10m	7d/wk-1a	15d	13-Mar-15 08	27-Mar-15 18	6d		EB, Inner Bench From West,CH 4045- 4055 = 10m							
A8750	EB, Inner Bench From West,CH 4055- 4065 = 10m	7d/wk-1a	15d	02-Apr-15 08	17-Apr-15 18	1d		EB, Inner Bench From West,CH 4055- 4065 = 10m							
A8755	EB, Inner Bench From West,CH 4065- 4075 = 10m	7d/wk-1a	15d	18-Apr-15 08	03-May-15 18	1d		EB, Inner Bench From West,CH 4065- 4075 = 10m							
A8760	EB, Inner Bench From West,CH 4075- 4085 = 10m	7d/wk-1a	15d	05-May-15 08	19-May-15 18	0d		EB, Inner Bench From West,CH 4075- 4085 = 10m							
A8761	EB, Inner Bench From West,CH 4085- 4095 = 10m	7d/wk-1a	15d	20-May-15 08	03-Jun-15 18	0d		EB, Inner Bench From West,CH 4085- 4095 = 10m							
From East (TS4)															
Inner Heading Excavation (3d/m, 24h/day work shift, 7d/week, no work on statutory holiday)															
A8835	EB,Inner Heading From East, CH 4147.5 to 4145 = 2.5m, @ 3d/m	7d/wk-1a	8d	06-Jan-15 08	13-Jan-15 18	0d		EB,Inner Heading From East, CH 4147.5 to 4145 = 2.5m, @ 3d/m							
A8850	EB,Inner Heading From East, CH 4145- 4135 = 10m, @ 3d/m	7d/wk-1a	30d	14-Jan-15 08	12-Feb-15 18	0d		EB,Inner Heading From East, CH 4145- 4135 = 10m, @ 3d/m							
A8830	EB,Inner Heading From East, CH 4135- 4125 = 10m @2d/m	7d/wk-1a	20d	13-Feb-15 08	07-Mar-15 18	0d		EB,Inner Heading From East, CH 4135- 4125 = 10m @2d/m							
A8840	EB,Inner Heading From East, CH 4125- 4115 = 10m @2d/m	7d/wk-1a	20d	08-Mar-15 08	27-Mar-15 18	0d		EB,Inner Heading From East, CH 4125- 4115 = 10m @2d/m							
A9910	EB,Inner Heading From East, CH 4115- 4105 = 10m @2d/m	7d/wk-1a	20d	28-Mar-15 08	17-Apr-15 18	0d		EB,Inner Heading From East, CH 4115- 4105 = 10m @2d/m							
A8845	EB,Inner Heading From East, CH 4105- 4095 = 10m @2d/m	7d/wk-1a	20d	18-Apr-15 08	08-May-15 18	0d		EB,Inner Heading From East, CH 4105- 4095 = 10m @2d/m							
Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)															
A8860	EB,Inner Bench From East, CH 4147.5 - 4145 = 2.5m	7d/wk-1a	4d	08-Mar-15 08	11-Mar-15 18	11d		EB,Inner Bench From East, CH 4147.5 - 4145 = 2.5m							

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

10 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2
A8865	EB,Inner Bench From East, CH 4145- 4135 = 10m	7d/wk-1a	15d	12-Mar-15 08	26-Mar-15 18	11d			■ EB,Inner Bench From East, CH 4145- 4135 = 10m				
A8870	EB,Inner Bench From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	28-Mar-15 08	12-Apr-15 18	10d			■ EB,Inner Bench From East, CH 4135- 4125 = 10m				
A8855	EB,Inner Bench From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	18-Apr-15 08	03-May-15 18	5d			■ EB,Inner Bench From East, CH 4125- 4115 = 10m				
A8875	EB,Inner Bench From East, CH 4115- 4105 = 10m	7d/wk-1a	15d	09-May-15 08	23-May-15 18	0d			■ EB,Inner Bench From East, CH 4115- 4105 = 10m				
A9915	EB,Inner Bench From East, CH 4105- 4095 = 10m	7d/wk-1a	16d	24-May-15 08	08-Jun-15 18	0d			■ EB,Inner Bench From East, CH 4105- 4095 = 10m				
Tunnel Lining Works													
From West Base Slab (10m/bay, 10m separation with benching excavation)													
A8900	EB From West, Base Slab CH 3990 - 3995 = 1 bay	7d/wk-1a	10d	04-Dec-14 08	13-Dec-14 18	33d			■ EB From West, Base Slab CH 3990 - 3995 = 1 bay				
A8890	EB From West, Base Slab CH 3995 - 4005 = 10m/bay	7d/wk-1a	10d	04-Jan-15 08	13-Jan-15 18	14d			■ EB From West, Base Slab CH 3995 - 4005 = 10m/bay				
A8905	EB From West, Base Slab CH 4005 - 4015 = 10m/bay	7d/wk-1a	10d	24-Jan-15 08	02-Feb-15 18	4d			■ EB From West, Base Slab CH 4005 - 4015 = 10m/bay				
A8910	EB From West, Base Slab CH 4015 - 4025 = 10m/bay	7d/wk-1a	10d	13-Feb-15 08	25-Feb-15 18	14d			■ EB From West, Base Slab CH 4015 - 4025 = 10m/bay				
A8915	EB From West, Base Slab CH 4025 - 4035 = 10m/bay	7d/wk-1a	10d	08-Mar-15 08	17-Mar-15 18	12d			■ EB From West, Base Slab CH 4025 - 4035 = 10m/bay				
A8920	EB From West, Base Slab CH 4035 - 4045 = 10m/bay	7d/wk-1a	10d	28-Mar-15 08	07-Apr-15 18	8d			■ EB From West, Base Slab CH 4035 - 4045 = 10m/bay				
A8925	EB From West, Base Slab CH 4045 - 4055 = 10m/bay	7d/wk-1a	10d	18-Apr-15 08	27-Apr-15 18	4d			■ EB From West, Base Slab CH 4045 - 4055 = 10m/bay				
A8930	EB From West, Base Slab CH 4055 - 4065 = 10m/bay	7d/wk-1a	10d	04-May-15 08	13-May-15 18	5d			■ EB From West, Base Slab CH 4055 - 4065 = 10m/bay				
A8880	EB From West, Base Slab CH 4065 - 4075 = 10m/bay	7d/wk-1a	10d	20-May-15 08	29-May-15 18	5d			■ EB From West, Base Slab CH 4065 - 4075 = 10m/bay				
A8885	EB From West, Base Slab CH 4075 - 4085 = 10m/bay	7d/wk-1a	10d	04-Jun-15 08	13-Jun-15 18	0d			■ EB From West, Base Slab CH 4075 - 4085 = 10m/bay				
A8895	EB From West, Base Slab CH 4085 - 4095 = 10m/bay	7d/wk-1a	10d	14-Jun-15 08	24-Jun-15 18	0d			■ EB From West, Base Slab CH 4085 - 4095 = 10m/bay				
From East Base Slab (10m/bay, 10m separation with benching excavation)													
A9905	EB From East, Base Slab CH 4149.5 - 4145 = 4.5m	7d/wk-1a	10d	13-Apr-15 08	22-Apr-15 18	26d			■ EB From East, Base Slab CH 4149.5 - 4145 = 4.5m				
A9900	EB From East, Base Slab CH 4145 - 4135 = 10m/bay	7d/wk-1a	10d	04-May-15 08	13-May-15 18	16d			■ EB From East, Base Slab CH 4145 - 4135 = 10m/bay				
A9895	EB From East, Base Slab CH 4135 - 4125 = 10m/bay	7d/wk-1a	10d	24-May-15 08	02-Jun-15 18	6d			■ EB From East, Base Slab CH 4135 - 4125 = 10m/bay				
A9890	EB From East, Base Slab CH 4125 - 4115 = 10m/bay	7d/wk-1a	10d	09-Jun-15 08	18-Jun-15 18	0d			■ EB From East, Base Slab CH 4125 - 4115 = 10m/bay				
A9885	EB From East, Base Slab CH 4115 - 4105 = 10m/bay	7d/wk-1a	10d	19-Jun-15 08	29-Jun-15 18	0d			■ EB From East, Base Slab CH 4115 - 4105 = 10m/bay				
A9880	EB From East, Base Slab CH 4105 - 4095 = 10m/bay	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d			■ EB From East, Base Slab CH 4105 - 4095 = 10m/bay				
Lining (5m/bay, 15m separation with base slab)													
A9065	EB From West, Lining CH 3990 - 3995 = 1bay	7d/wk-1a	10d	03-Feb-15 08	12-Feb-15 18	4d			■ EB From West, Lining CH 3990 - 3995 = 1bay				
A9005	EB From West, Lining CH 3995 - 4000 = 1bay	7d/wk-1a	10d	13-Feb-15 08	25-Feb-15 18	4d			■ EB From West, Lining CH 3995 - 4000 = 1bay				
A9090	EB From West, Lining CH 4000 - 4005 = 1bay	7d/wk-1a	10d	26-Feb-15 08	07-Mar-15 18	4d			■ EB From West, Lining CH 4000 - 4005 = 1bay				
Summary Bar							Prepared by William Caluza						
Actual Level of Effort							Date	Revision	Checked	Approved			
Actual Work							26-Sep...	1st submission					
Remaining Work													
Critical Remaining Work													
Milestone													
11 of 18													
China State Construction Engineering (Hong Kong) Ltd													
Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)													
WORKS PROGRAMME REV. M													

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015					2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A9050	EB From West, Lining CH 4005 - 4010 = 1bay	7d/wk-1a	10d	08-Mar-15 08	17-Mar-15 18	4d			■ EB From West, Lining CH 4005 - 4010 = 1bay					
A9055	EB From West, Lining CH 4010 - 4015 = 1bay	7d/wk-1a	10d	18-Mar-15 08	27-Mar-15 18	4d			■ EB From West, Lining CH 4010 - 4015 = 1bay					
A9060	EB From West, Lining CH 4015 - 4020 = 1bay	7d/wk-1a	10d	26-Mar-15 08	05-Apr-15 18	4d			■ EB From West, Lining CH 4015 - 4020 = 1bay					
A9070	EB From West, Lining CH 4020 - 4025 = 1bay	7d/wk-1a	10d	03-Apr-15 08	13-Apr-15 18	4d			■ EB From West, Lining CH 4020 - 4025 = 1bay					
A9075	EB From West, Lining CH 4025 - 4030 = 1bay	7d/wk-1a	10d	12-Apr-15 08	21-Apr-15 18	4d			■ EB From West, Lining CH 4025 - 4030 = 1bay					
A9080	EB From West, Lining CH 4030 - 4035 = 1bay	7d/wk-1a	10d	20-Apr-15 08	29-Apr-15 18	4d			■ EB From West, Lining CH 4030 - 4035 = 1bay					
A9085	EB From West, Lining CH 4035 - 4040 = 1bay	7d/wk-1a	10d	28-Apr-15 08	08-May-15 18	4d			■ EB From West, Lining CH 4035 - 4040 = 1bay					
A9015	EB From West, Lining CH 4040 - 4045 = 1bay	7d/wk-1a	10d	07-May-15 08	16-May-15 18	4d			■ EB From West, Lining CH 4040 - 4045 = 1bay					
A9020	EB From West, Lining CH 4045 - 4050 = 1bay	7d/wk-1a	10d	15-May-15 08	24-May-15 18	4d			■ EB From West, Lining CH 4045 - 4050 = 1bay					
A9025	EB From West, Lining CH 4050 - 4055 = 1bay	7d/wk-1a	10d	23-May-15 08	01-Jun-15 18	4d			■ EB From West, Lining CH 4050 - 4055 = 1bay					
A9030	EB From West, Lining CH 4055 - 4060 = 1bay	7d/wk-1a	10d	31-May-15 08	09-Jun-15 18	4d			■ EB From West, Lining CH 4055 - 4060 = 1bay					
A9035	EB From West, Lining CH 4060 - 4065 = 1bay	7d/wk-1a	10d	07-Jun-15 08	16-Jun-15 18	4d			■ EB From West, Lining CH 4060 - 4065 = 1bay					
A9040	EB From West, Lining CH 4065 - 4070 = 1bay	7d/wk-1a	10d	14-Jun-15 08	24-Jun-15 18	4d			■ EB From West, Lining CH 4065 - 4070 = 1bay					
A9045	EB From West, Lining CH 4070 - 4075 = 1bay	7d/wk-1a	10d	25-Jun-15 08	05-Jul-15 18	0d			■ EB From West, Lining CH 4070 - 4075 = 1bay					
A8955	EB From West, Lining CH 4075 - 4080 = 1bay	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d			■ EB From West, Lining CH 4075 - 4080 = 1bay					
A8960	EB From West, Lining CH 4080 - 4085 = 1bay	7d/wk-1a	5d	11-Jul-15 08	15-Jul-15 18	0d			■ EB From West, Lining CH 4080 - 4085 = 1bay					
A8970	EB From West, Lining CH 4085 - 4090 = 1bay	7d/wk-1a	5d	16-Jul-15 08	20-Jul-15 18	0d			■ EB From West, Lining CH 4085 - 4090 = 1bay					
A8975	EB From West, Lining CH 4090 - 4095 = 1bay	7d/wk-1a	5d	21-Jul-15 08	25-Jul-15 18	0d			■ EB From West, Lining CH 4090 - 4095 = 1bay					
A8980	EB From West, Lining CH 4095 - 4100 = 1bay	7d/wk-1a	5d	26-Jul-15 08	30-Jul-15 18	0d			■ EB From West, Lining CH 4095 - 4100 = 1bay					
A8985	EB From West, Lining CH 4100 - 4105 = 1bay	7d/wk-1a	5d	31-Jul-15 08	04-Aug-15 18	0d			■ EB From West, Lining CH 4100 - 4105 = 1bay					
A8990	EB From West, Lining CH 4105 - 4110 = 1bay	7d/wk-1a	5d	05-Aug-15 08	09-Aug-15 18	0d			■ EB From West, Lining CH 4105 - 4110 = 1bay					
A8995	EB From West, Lining CH 4110 - 4115 = 1bay	7d/wk-1a	5d	10-Aug-15 08	14-Aug-15 18	0d			■ EB From West, Lining CH 4110 - 4115 = 1bay					
A9000	EB From West, Lining CH 4115 - 4120 = 1bay	7d/wk-1a	5d	15-Aug-15 08	19-Aug-15 18	0d			■ EB From West, Lining CH 4115 - 4120 = 1bay					
A9010	EB From West, Lining CH 4120 - 4125 = 1bay	7d/wk-1a	5d	20-Aug-15 08	24-Aug-15 18	0d			■ EB From West, Lining CH 4120 - 4125 = 1bay					
A8965	EB From West, Lining CH 4125 - 4130 = 1bay	7d/wk-1a	5d	25-Aug-15 08	29-Aug-15 18	0d			■ EB From West, Lining CH 4125 - 4130 = 1bay					
A8935	EB From West, Lining CH 4130 - 4135 = 1bay	7d/wk-1a	5d	30-Aug-15 08	03-Sep-15 18	0d			■ EB From West, Lining CH 4130 - 4135 = 1bay					
A8940	EB From West, Lining CH 4135 - 4140 = 1bay	7d/wk-1a	5d	04-Sep-15 08	08-Sep-15 18	0d			■ EB From West, Lining CH 4135 - 4140 = 1bay					
A8945	EB From West, Lining CH 4140 - 4145 = 1bay	7d/wk-1a	5d	09-Sep-15 08	13-Sep-15 18	0d			■ EB From West, Lining CH 4140 - 4145 = 1bay					
A8950	EB From West, Lining CH 4145 - 4149.5 = 4.5m	7d/wk-1a	5d	14-Sep-15 08	18-Sep-15 18	0d			■ EB From West, Lining CH 4145 - 4149.5 = 4.5m					

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

12 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		

中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015							2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3		
OHVD(10m/bay) / Utility Trough																
A9095	EB From West OHVD and utility trough =, 167= 17 bays @ 10m/bay @ 7d/bay	7d/wk-1a	120d	03-Jul-15 08	02-Nov-15 18	0d	<div></div> EB From West OHVD and utility trough =, 167= 17 bays @ 10									
WB Outer Tunnel Excavation																
From West (TPCWAE)																
Outer Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																
A9651	WB, Outer Heading From West, CH 4085- 4092.5 = 7.5m @ 2d/m	7d/wk-1a	15d	13-Sep-14 08 A	30-Sep-14 18	163d	<div></div> WB, Outer Heading From West, CH 4085- 4092.5 = 7.5m @ 2d/m									
Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)																
A9680	WB, Outer Bench From West, CH 4025- 4035 = 10m	7d/wk-1a	15d	12-Oct-14 08	26-Oct-14 18	163d	<div></div> WB, Outer Bench From West, CH 4025- 4035 = 10m									
A9665	WB, Outer Bench From West, CH 4035- 4045 = 10m	7d/wk-1a	15d	27-Oct-14 08	10-Nov-14 18	163d	<div></div> WB, Outer Bench From West, CH 4035- 4045 = 10m									
A9670	WB, Outer Bench From West, CH 4045- 4055 = 10m	7d/wk-1a	15d	11-Nov-14 08	25-Nov-14 18	163d	<div></div> WB, Outer Bench From West, CH 4045- 4055 = 10m									
A9675	WB, Outer Bench From West, CH 4055- 4065 = 10m	7d/wk-1a	15d	26-Nov-14 08	10-Dec-14 18	163d	<div></div> WB, Outer Bench From West, CH 4055- 4065 = 10m									
A9700	WB, Outer Bench From West, CH 4065- 4075 = 10m	7d/wk-1a	15d	11-Dec-14 08	26-Dec-14 18	163d	<div></div> WB, Outer Bench From West, CH 4065- 4075 = 10m									
A9701	WB, Outer Bench From West, CH 4075- 4082.5 = 7.5m	7d/wk-1a	15d	27-Dec-14 08	11-Jan-15 18	163d	<div></div> WB, Outer Bench From West, CH 4075- 4082.5 = 7.5m									
From East (TS4)																
Outer Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																
A9730	WB, Outer Heading From East, CH 4105- 4092.5 = 12.5m @2d/m	7d/wk-1a	25d	30-Aug-14 08 A	30-Sep-14 18	168d	<div></div> WB, Outer Heading From East, CH 4105- 4092.5 = 12.5m @2d/m									
Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)																
A9740	WB, Outer Bench From East, CH 4136- 4135 = 1m	7d/wk-1a	2d	12-Oct-14 08	13-Oct-14 18	168d	<div></div> WB, Outer Bench From East, CH 4136- 4135 = 1m									
A9770	WB, Outer Bench From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	14-Oct-14 08	28-Oct-14 18	168d	<div></div> WB, Outer Bench From East, CH 4135- 4125 = 10m									
A9745	WB, Outer Bench From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	28-Oct-14 08	11-Nov-14 18	168d	<div></div> WB, Outer Bench From East, CH 4125- 4115 = 10m									
A9750	WB, Outer Bench From East, CH 4115- 4105 = 10m	7d/wk-1a	15d	11-Nov-14 08	25-Nov-14 18	168d	<div></div> WB, Outer Bench From East, CH 4115- 4105 = 10m									
A9755	WB, Outer Bench From East, CH 4105- 4095 = 10m	7d/wk-1a	15d	26-Nov-14 08	10-Dec-14 18	168d	<div></div> WB, Outer Bench From East, CH 4105- 4095 = 10m									
A9760	WB, Outer Bench From East, CH 4095- 4082.5 = 12.5m	7d/wk-1a	25d	11-Dec-14 08	06-Jan-15 18	168d	<div></div> WB, Outer Bench From East, CH 4095- 4082.5 = 12.5m									
WB (Inner Tunnel Excavation + Lining)																
From West (TPCWAE)																
Inner Heading Excavation (2-3d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																
A9130	WB, Inner Heading From West, CH 3993- 4005 = 12m @3d/m	7d/wk-1a	50d	29-Sep-14 08	18-Nov-14 18	0d	<div></div> WB, Inner Heading From West, CH 3993- 4005 = 12m @3d/m									
A9135	WB, Inner Heading From West, CH 4005- 4015 = 10m @2d/m	7d/wk-1a	20d	19-Nov-14 08	08-Dec-14 18	0d	<div></div> WB, Inner Heading From West, CH 4005- 4015 = 10m @2d/m									
A9140	WB, Inner Heading From West, CH 4015- 4025 = 10m @2d/m	7d/wk-1a	20d	09-Dec-14 08	29-Dec-14 18	0d	<div></div> WB, Inner Heading From West, CH 4015- 4025 = 10m @2d/m									

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

13 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2016												
							Q4			Q1	Q2	Q3	Q4	Q1	Q2	Q3			
A9100	WB,Inner Heading From West, CH 4025- 4035 = 10m @2d/m	7d/wk-1a	20d	30-Dec-14 08	19-Jan-15 18	0d			WB,Inner Heading From West, CH 4025- 4035 = 10m @2d/m										
A9105	WB,Inner Heading From West, CH 4035- 4045 = 10m @2d/m	7d/wk-1a	20d	20-Jan-15 08	08-Feb-15 18	0d			WB,Inner Heading From West, CH 4035- 4045 = 10m @2d/m										
A9110	WB,Inner Heading From West, CH 4045- 4055 = 10m @2d/m	7d/wk-1a	20d	09-Feb-15 08	03-Mar-15 18	0d			WB,Inner Heading From West, CH 4045- 4055 = 10m @2d/m										
A9115	WB,Inner Heading From West, CH 4055- 4065 = 10m @ 2d/m	7d/wk-1a	20d	04-Mar-15 08	23-Mar-15 18	0d			WB,Inner Heading From West, CH 4055- 4065 = 10m @ 2d/m										
A9120	WB,Inner Heading From West, CH 4065- 4075 = 10m, @ 2d/m	7d/wk-1a	20d	24-Mar-15 08	13-Apr-15 18	0d			WB,Inner Heading From West, CH 4065- 4075 = 10m, @ 2d/m										
A9125	WB,Inner Heading From West, CH 4075- 4085 = 10m @ 2d/m	7d/wk-1a	20d	14-Apr-15 08	04-May-15 18	0d			WB,Inner Heading From West, CH 4075- 4085 = 10m @ 2d/m										
Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)																			
A9180	WB,Inner Bench From West, CH 3993- 4005 = 12m	7d/wk-1a	18d	30-Dec-14 08	17-Jan-15 18	27d			WB,Inner Bench From West, CH 3993- 4005 = 12m										
A9205	WB,Inner Bench From West, CH 4005- 4015 = 10m	7d/wk-1a	15d	20-Jan-15 08	03-Feb-15 18	25d			WB,Inner Bench From West, CH 4005- 4015 = 10m										
A9190	WB,Inner Bench From West, CH 4015- 4025 = 10m	7d/wk-1a	15d	09-Feb-15 08	26-Feb-15 18	20d			WB,Inner Bench From West, CH 4015- 4025 = 10m										
A9185	WB,Inner Bench From West, CH 4025- 4035 = 10m	7d/wk-1a	15d	04-Mar-15 08	18-Mar-15 18	15d			WB,Inner Bench From West, CH 4025- 4035 = 10m										
A9155	WB,Inner Bench From West, CH 4035- 4045 = 10m	7d/wk-1a	15d	24-Mar-15 08	08-Apr-15 18	10d			WB,Inner Bench From West, CH 4035- 4045 = 10m										
A9160	WB,Inner Bench From West, CH 4045- 4055 = 10m	7d/wk-1a	15d	14-Apr-15 08	28-Apr-15 18	5d			WB,Inner Bench From West, CH 4045- 4055 = 10m										
A9165	WB,Inner Bench From West, CH 4055- 4065 = 10m	7d/wk-1a	15d	05-May-15 08	19-May-15 18	0d			WB,Inner Bench From West, CH 4055- 4065 = 10m										
A9170	WB,Inner Bench From West, CH 4065- 4075 = 10m	7d/wk-1a	15d	20-May-15 08	03-Jun-15 18	0d			WB,Inner Bench From West, CH 4065- 4075 = 10m										
A9175	WB,Inner Bench From West, CH 4075- 4085 = 10m	7d/wk-1a	15d	04-Jun-15 08	18-Jun-15 18	0d			WB,Inner Bench From West, CH 4075- 4085 = 10m										
From East (TS4)																			
Inner Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																			
A9210	WB,Inner Heading From East, CH 4135- 4125 = 10m @2d/m	7d/wk-1a	20d	14-Jan-15 08	02-Feb-15 18	6d			WB,Inner Heading From East, CH 4135- 4125 = 10m @2d/m										
A9215	WB,Inner Heading From East, CH 4125- 4115 = 10m @2d/m	7d/wk-1a	20d	03-Feb-15 08	25-Feb-15 18	6d			WB,Inner Heading From East, CH 4125- 4115 = 10m @2d/m										
A9230	WB,Inner Heading From East, CH 4115- 4105 = 10m @2d/m	7d/wk-1a	20d	26-Feb-15 08	17-Mar-15 18	6d			WB,Inner Heading From East, CH 4115- 4105 = 10m @2d/m										
A9232	WB,Inner Heading From East, CH 4105- 4095 = 10m @2d/m	7d/wk-1a	20d	18-Mar-15 08	07-Apr-15 18	6d			WB,Inner Heading From East, CH 4105- 4095 = 10m @2d/m										
A9225	WB,Inner Heading From East, CH 4095- 4085 = 10m @2d/m	7d/wk-1a	20d	08-Apr-15 08	27-Apr-15 18	6d			WB,Inner Heading From East, CH 4095- 4085 = 10m @2d/m										
Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)																			
A9235	WB,Inner Bench From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	18-Mar-15 08	01-Apr-15 18	16d			WB,Inner Bench From East, CH 4135- 4125 = 10m										
A9240	WB,Inner Bench From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	08-Apr-15 08	22-Apr-15 18	11d			WB,Inner Bench From East, CH 4125- 4115 = 10m										
A9245	WB,Inner Bench From East, CH 4115- 4105 = 10m	7d/wk-1a	15d	28-Apr-15 08	13-May-15 18	6d			WB,Inner Bench From East, CH 4115- 4105 = 10m										
A9247	WB,Inner Bench From East, CH 4105- 4095 = 10m	7d/wk-1a	15d	14-May-15 08	28-May-15 18	6d			WB,Inner Bench From East, CH 4105- 4095 = 10m										
A9250	WB,Inner Bench From East, CH 4095- 4085 = 10m	7d/wk-1a	15d	29-May-15 08	12-Jun-15 18	6d			WB,Inner Bench From East, CH 4095- 4085 = 10m										

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

14 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float									
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
Tunnel Lining Works															
From West Base Slab (10m/bay, 10m separation with benching excavation)															
A9295	WB From West, Base Slab CH 3990 - 3995 = 5m bay	7d/wk-1a	10d	18-Jan-15 08	27-Jan-15 18	37d	■ WB From West, Base Slab CH 3990 - 3995 = 5m bay								
A9320	WB From West, Base Slab CH 3995 - 4005 = 10m/bay	7d/wk-1a	10d	04-Feb-15 08	13-Feb-15 18	30d	■ WB From West, Base Slab CH 3995 - 4005 = 10m/bay								
A9255	WB From West, Base Slab CH 4005 - 4015 = 10m/bay	7d/wk-1a	10d	27-Feb-15 08	08-Mar-15 18	50d	■ WB From West, Base Slab CH 4005 - 4015 = 10m/bay								
A9260	WB From West, Base Slab CH 4015 - 4025 = 10m/bay	7d/wk-1a	10d	19-Mar-15 08	28-Mar-15 18	40d	■ WB From West, Base Slab CH 4015 - 4025 = 10m/bay								
A9265	WB From West, Base Slab CH 4025 - 4035 = 10m/bay	7d/wk-1a	10d	09-Apr-15 08	18-Apr-15 18	30d	■ WB From West, Base Slab CH 4025 - 4035 = 10m/bay								
A9300	WB From West, Base Slab CH 4035 - 4045 = 10m/bay	7d/wk-1a	10d	29-Apr-15 08	09-May-15 18	20d	■ WB From West, Base Slab CH 4035 - 4045 = 10m/bay								
A9325	WB From West, Base Slab CH 4045 - 4055 = 10m/bay	7d/wk-1a	10d	20-May-15 08	29-May-15 18	10d	■ WB From West, Base Slab CH 4045 - 4055 = 10m/bay								
A9305	WB From West, Base Slab CH 4055 - 4065 = 10m/bay	7d/wk-1a	10d	04-Jun-15 08	13-Jun-15 18	5d	■ WB From West, Base Slab CH 4055 - 4065 = 10m/bay								
A9310	WB From West, Base Slab CH 4065 - 4075 = 10m/bay	7d/wk-1a	10d	19-Jun-15 08	29-Jun-15 18	0d	■ WB From West, Base Slab CH 4065 - 4075 = 10m/bay								
A9315	WB From West, Base Slab CH 4075 - 4080 = 5m	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d	■ WB From West, Base Slab CH 4075 - 4080 = 5m								
From East Base Slab (10m/bay, 10m separation with benching excavation)															
A9960	WB From East, Base Slab CH 4135 - 4125 = 10m/bay	7d/wk-1a	10d	23-Apr-15 08	03-May-15 18	26d	■ WB From East, Base Slab CH 4135 - 4125 = 10m/bay								
A9955	WB From East, Base Slab CH 4125 - 4115 = 10m/bay	7d/wk-1a	10d	14-May-15 08	23-May-15 18	16d	■ WB From East, Base Slab CH 4125 - 4115 = 10m/bay								
A9950	WB From East, Base Slab CH 4115 - 4105 = 10m/bay	7d/wk-1a	10d	29-May-15 08	07-Jun-15 18	11d	■ WB From East, Base Slab CH 4115 - 4105 = 10m/bay								
A9945	WB From East, Base Slab CH 4105 - 4095 = 10m/bay	7d/wk-1a	10d	13-Jun-15 08	23-Jun-15 18	6d	■ WB From East, Base Slab CH 4105 - 4095 = 10m/bay								
A9940	WB From East, Base Slab CH 4095 - 4085 = 10m/bay	7d/wk-1a	10d	24-Jun-15 08	04-Jul-15 18	6d	■ WB From East, Base Slab CH 4095 - 4085 = 10m/bay								
A9941	WB From East, Base Slab CH 4085 - 4080 = 5m	7d/wk-1a	10d	05-Jul-15 08	14-Jul-15 18	6d	■ WB From East, Base Slab CH 4085 - 4080 = 5m								
Lining (5m/bay, 10m separation with base slab)															
A9430	WB From West, Lining CH 3990 - 3995 = 1bay	7d/wk-1a	7d	14-Feb-15 08	23-Feb-15 18	30d	■ WB From West, Lining CH 3990 - 3995 = 1bay								
A9470	WB From West, Lining CH 3995 - 4000 = 1bay	7d/wk-1a	7d	24-Feb-15 08	02-Mar-15 18	30d	■ WB From West, Lining CH 3995 - 4000 = 1bay								
A9435	WB From West, Lining CH 4000 - 4005 = 1bay	7d/wk-1a	7d	03-Mar-15 08	09-Mar-15 18	30d	■ WB From West, Lining CH 4000 - 4005 = 1bay								
A9360	WB From West, Lining CH 4005 - 4010 = 1bay	7d/wk-1a	7d	10-Mar-15 08	16-Mar-15 18	30d	■ WB From West, Lining CH 4005 - 4010 = 1bay								
A9365	WB From West, Lining CH 4010 - 4015 = 1bay	7d/wk-1a	7d	17-Mar-15 08	23-Mar-15 18	30d	■ WB From West, Lining CH 4010 - 4015 = 1bay								
A9370	WB From West, Lining CH 4015 - 4020 = 1bay	7d/wk-1a	7d	24-Mar-15 08	30-Mar-15 18	30d	■ WB From West, Lining CH 4015 - 4020 = 1bay								
A9375	WB From West, Lining CH 4020 - 4025 = 1bay	7d/wk-1a	7d	31-Mar-15 08	07-Apr-15 18	30d	■ WB From West, Lining CH 4020 - 4025 = 1bay								
A9380	WB From West, Lining CH 4025 - 4030 = 1bay	7d/wk-1a	7d	08-Apr-15 08	14-Apr-15 18	30d	■ WB From West, Lining CH 4025 - 4030 = 1bay								
A9385	WB From West, Lining CH 4030 - 4035 = 1bay	7d/wk-1a	7d	15-Apr-15 08	21-Apr-15 18	30d	■ WB From West, Lining CH 4030 - 4035 = 1bay								

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

15 of 18


China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		

中國建築工程(香港)有限公司

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015									2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
A9390	WB From West, Lining CH 4035 - 4040 = 1bay	7d/wk-1a	7d	22-Apr-15 08	28-Apr-15 18	30d				■ WB From West, Lining CH 4035 - 4040 = 1bay								
A9330	WB From West, Lining CH 4040 - 4045 = 1bay	7d/wk-1a	7d	29-Apr-15 08	06-May-15 18	30d				■ WB From West, Lining CH 4040 - 4045 = 1bay								
A9335	WB From West, Lining CH 4045 - 4050 = 1bay	7d/wk-1a	7d	07-May-15 08	13-May-15 18	30d				■ WB From West, Lining CH 4045 - 4050 = 1bay								
A9340	WB From West, Lining CH 4050 - 4055 = 1bay	7d/wk-1a	7d	14-May-15 08	20-May-15 18	30d				■ WB From West, Lining CH 4050 - 4055 = 1bay								
A9345	WB From West, Lining CH 4055 - 4060 = 1bay	7d/wk-1a	7d	21-May-15 08	27-May-15 18	30d				■ WB From West, Lining CH 4055 - 4060 = 1bay								
A9350	WB From West, Lining CH 4060 - 4065 = 1bay	7d/wk-1a	7d	28-May-15 08	03-Jun-15 18	30d				■ WB From West, Lining CH 4060 - 4065 = 1bay								
A9355	WB From West, Lining CH 4065 - 4070 = 1bay	7d/wk-1a	5d	04-Jun-15 08	08-Jun-15 18	30d				■ WB From West, Lining CH 4065 - 4070 = 1bay								
A9415	WB From West, Lining CH 4070 - 4075 = 1bay	7d/wk-1a	5d	11-Jul-15 08	15-Jul-15 18	0d				■ WB From West, Lining CH 4070 - 4075 = 1bay								
A9475	WB From West, Lining CH 4075 - 4080 = 1bay	7d/wk-1a	5d	16-Jul-15 08	20-Jul-15 18	0d				■ WB From West, Lining CH 4075 - 4080 = 1bay								
A9440	WB From West, Lining CH 4080 - 4085 = 1bay	7d/wk-1a	5d	21-Jul-15 08	25-Jul-15 18	0d				■ WB From West, Lining CH 4080 - 4085 = 1bay								
A9445	WB From West, Lining CH 4085 - 4090 = 1bay	7d/wk-1a	5d	26-Jul-15 08	30-Jul-15 18	0d				■ WB From West, Lining CH 4085 - 4090 = 1bay								
A9450	WB From West, Lining CH 4090 - 4095 = 1bay	7d/wk-1a	5d	31-Jul-15 08	04-Aug-15 18	0d				■ WB From West, Lining CH 4090 - 4095 = 1bay								
A9455	WB From West, Lining CH 4095 - 4100 = 1bay	7d/wk-1a	5d	05-Aug-15 08	09-Aug-15 18	0d				■ WB From West, Lining CH 4095 - 4100 = 1bay								
A9420	WB From West, Lining CH 4100 - 4105 = 1bay	7d/wk-1a	5d	10-Aug-15 08	14-Aug-15 18	0d				■ WB From West, Lining CH 4100 - 4105 = 1bay								
A9425	WB From West, Lining CH 4105 - 4110 = 1bay	7d/wk-1a	5d	15-Aug-15 08	19-Aug-15 18	0d				■ WB From West, Lining CH 4105 - 4110 = 1bay								
A9460	WB From West, Lining CH 4110 - 4115 = 1bay	7d/wk-1a	5d	20-Aug-15 08	24-Aug-15 18	0d				■ WB From West, Lining CH 4110 - 4115 = 1bay								
A9465	WB From West, Lining CH 4115 - 4120 = 1bay	7d/wk-1a	5d	25-Aug-15 08	29-Aug-15 18	0d				■ WB From West, Lining CH 4115 - 4120 = 1bay								
A9395	WB From West, Lining CH 4120 - 4125 = 1bay	7d/wk-1a	5d	30-Aug-15 08	03-Sep-15 18	0d				■ WB From West, Lining CH 4120 - 4125 = 1bay								
A9400	WB From West, Lining CH 4125 - 4130 = 1bay	7d/wk-1a	5d	04-Sep-15 08	08-Sep-15 18	0d				■ WB From West, Lining CH 4125 - 4130 = 1bay								
A9405	WB From West, Lining CH 4130 - 4135 = 1bay	7d/wk-1a	5d	09-Sep-15 08	13-Sep-15 18	0d				■ WB From West, Lining CH 4130 - 4135 = 1bay								
A9410	WB From West, Lining CH 4135 - 4136.5 = 1bay	7d/wk-1a	5d	14-Sep-15 08	18-Sep-15 18	0d				■ WB From West, Lining CH 4135 - 4136.5 = 1bay								
OHVD(10m/bay) / Utility Trough																		
A9480	WB From West OHVD and utility trough =, 153= 16 bays @ 10m/bay @ 7d/bay	7d/wk-1a	115d	08-Jul-15 08	02-Nov-15 18	0d				■ WB From West OHVD and utility trough =, 153= 16 bays @ 10m/bay @ 7d/bay								
Completion of KD10- Section 5																		
A8445	KD10- Section 2: Completion of Mined Tunnel Works (orig. Target KD10- 2 Nov 2015)	7d/wk-2	0d		02-Nov-15 18*	0d					◆ KD10- Section 2: Completion of Mined Tunnel Works (orig. Target KD10- 2 Nov 2015)							
Interface works with other Contracts																		
S5_60115	Handover TZ6 to MTR	7d/wk-2	0d		30-Sep-14 18	-249d	◆ Handover TZ6 to MTR											
S6_5283	Handover TZ4 to CWB(T2)	7d/wk-2	0d		10-Nov-14 18	-290d	◆ Handover TZ4 to CWB(T2)											
S6_5275	Provide access to CWB (CC) Contractor- TS1 & TS2	7d/wk-2	0d		21-Nov-14 18*	-85d	◆ Provide access to CWB (CC) Contractor- TS1 & TS2											
16 of 18							Prepared by William Caluza											
China State Construction Engineering (Hong Kong) Ltd							Date	Revision	Checked	Approved								
Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)							26-Sep...	1st submission										
WORKS PROGRAMME REV. M																		
Summary Bar																		
Actual Level of Effort																		
Actual Work																		
Remaining Work																		
Critical Remaining Work																		
◆ Milestone																		

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2
SB_5280	Provide access to CWB (CC) Contractor- TS4, TPCWA, Mined Tunnel	7d/wk-2	0d		31-Mar-16 18*	-124d							◆ Provide access to CWB (CC) Contractor
Stage and Section Completion													
KD_5735	KD8 - Completion of Section 3, (1326d)	7d/wk-2	0d		30-Sep-14 18*	-86d	◆ KD8 - Completion of Section 3, (1326d)						
KD_5720	KD5 - Achievement of Stage 5, (1152d)	7d/wk-2	0d		16-Oct-14 18*	-323d	◆ KD5 - Achievement of Stage 5, (1152d)						
KD_5760	KD13 - Completion of Section 7B, (1152d)	7d/wk-2	0d		17-Nov-14 18*	-353d	◆ KD13 - Completion of Section 7B, (1152d)						
KD_5730	KD7 - Completion of Section 2, (1152d)	7d/wk-2	0d		17-Nov-14 18*	-297d	◆ KD7 - Completion of Section 2, (1152d)						
KD_5740	KD9 - Completion of Section 4, (1739d)	7d/wk-2	0d		10-Nov-15 18*	-132d				◆ KD9 - Completion of Section 4, (1739d)			
KD_5745	KD10 - Completion of Section 5, (1863d)	7d/wk-2	0d		25-Mar-16 18	-144d				◆ KD10 - Completion of Section 5, (1863d)			
KD_5750	KD11 - Completion of Section 6, (1949d)	7d/wk-2	0d		23-May-16 18*	-121d				◆ KD11 - Completion of Section 6, (1949d)			
Portion Handover Date													
CD_5685	Portion Handover - Portion IV(4), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion IV(4), KD8 +28						
CD_5680	Portion Handover - Portion V (5), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion V (5), KD8 +28						
CD_5695	Portion Handover - Portion VI (6), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion VI (6), KD8 +28						
CD_5735	Portion Handover - Portion XIII B (13B), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion XIII B (13B), KD8 +28						
CD_5790	Portion Handover - Portion XXII (22), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion XXII (22), KD8 +28						
CD_5670	Portion Handover - Portion III (3), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion III (3), KD8 +28						
CD_5720	Portion Handover - Portion XIII A (13A), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XIII A (13A), KD7 +28						
CD_5705	Portion Handover - Portion VIII (8), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion VIII (8), KD7 +28						
CD_5730	Portion Handover - Portion XIVA (14A), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XIVA (14A), KD7 +28						
CD_5740	Portion Handover - Portion XV (15), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XV (15), KD7 +28						
CD_5805	Portion Handover - Portion XXIII (23), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XXIII (23), KD7 +28						
CD_5775	Portion Handover - Portion XVIII (18), KD10 +28	7d/wk-2	0d		30-Nov-15 18*	0d				◆ Portion Handover - Portion XVIII (18), KD10 +28			
CD_5710	Portion Handover - Portion XI (11), KD9 +28	7d/wk-2	0d		27-Dec-15 18*	0d				◆ Portion Handover - Portion XI (11), KD9 +28			
CD_5700	Portion Handover - Portion IX (9), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d				◆ Portion Handover - Portion IX (9), KD10 +28			
CD_5745	Portion Handover - Portion XIV B (14B), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d				◆ Portion Handover - Portion XIV B (14B), KD10 +28			
CD_5755	Portion Handover - Portion XVI (16), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d				◆ Portion Handover - Portion XVI (16), KD10 +28			
CD_5750	Portion Handover - Portion XVII (17), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d				◆ Portion Handover - Portion XVII (17), KD10 +28			
CD_5760	Portion Handover - Portion XIX (19), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d				◆ Portion Handover - Portion XIX (19), KD10 +28			
CD_5780	Portion Handover - Portion XX B (20B), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d				◆ Portion Handover - Portion XX B (20B), KD10 +28			

Summary Bar

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

◆

◆ Milestone

17 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
25-Sep...	1st submission		

中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015					2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
CD_5690	Portion Handover - Portion VII (7), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5725	Portion Handover - Portion XII (12), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5715	Portion Handover - Portion X (10), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5785	Portion Handover - Portion XXA (20A), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5795	Portion Handover - Portion XXI (21), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov

 Summary Bar
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone

18 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel (Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司
 CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Early Start	Early Finish	Remaining Duration	Activity % Complete		Mar	2015 Apr	May	Jun
HK/2012/08 Revised Works Programme Rev.4 (Revised as of 28-Feb-15)										
Dredging and Reclamation										
Marine Work Construction										
Zone A2										
Seawall Construction - Zone A2										
MAR10775	Zone A2 - seawall - Type 4, 13 - lay toe block and leveling stone in line with backfilling in zone A2(2)	19-May-15*	02-Jun-15	15	0%					
Zone D										
Seawall Construction - Zone D										
Seawall 2C-L										
MAR12263	Zone D - TTA for demolish existing seawall	28-Feb-15	19-Mar-15	17	0%					
MAR12264	Zone D - Preparation Works & demolish existing seawall	20-Mar-15	02-Sep-15	135	0%					
Works for Section Completion										
Construction										
Section II - MVB Structure										
MVB Substructure - Diaphragm Wall for Portion A&B										
MVB A&B - Pumping Test Preparation/ Pumping Test										
SII10580	Sec II - MVB A&B - pumping test	20-Mar-15*	31-Mar-15	12	0%					
MVB Substructure - ELS & Structural Works for Portion A										
MVB Substructure - ELS for Portion A										
SII10840	Sec II - MVB A - Install Strut L1 at +2.7mPD	10-Feb-15 A	04-Mar-15	4	55.56%					
SII10860	Sec II - MVB A - Excavation down to -1.5mPD	28-Feb-15 A	25-Mar-15	22	0%					
SII10880	Sec II - MVB A - Install Strut L2 at -1.0mPD	05-Mar-15	31-Mar-15	23	0%					
SII10900	Sec II - MVB A - Excavation down to -6.5mPD	25-Mar-15	21-Apr-15	20	0%					
SII10920	Sec II - MVB A - Install Strut L3 at -5.5mPD	01-Apr-15	27-Apr-15	19	0%					
SII10940	Sec II - MVB A - Excavation down to -10.5mPD	22-Apr-15	11-May-15	16	0%					
SII10960	Sec II - MVB A - Install Strut L4 at -9.5mPD	28-Apr-15	23-May-15	22	0%					
SII10980	Sec II - MVB A - Excavation down to -14mPD	14-May-15	30-May-15	14	0%					
SII11000	Sec II - MVB A - Install Strut L5 at -13mPD	19-May-15	12-Jun-15	21	0%					
MVB Substructure - ELS & Structural Works for Portion B										
MVB Substructure - ELS for Portion B										
SII11460	Sec II - MVB B: Install Strut L1 at +2.7mPD	12-Feb-15 A	04-Mar-15	4	55.56%					
SII11480	Sec II - MVB B: Excavation down to -1.0mPD	28-Feb-15 A	25-Mar-15	22	0%					
SII11500	Sec II - MVB B: Install Strut L2 at 0.0mPD	05-Mar-15	31-Mar-15	23	0%					
SII11520	Sec II - MVB B: Excavation down to -5.5mPD	25-Mar-15	21-Apr-15	20	0%					
SII11540	Sec II - MVB B: Install Strut L3 at -4.5mPD	01-Apr-15	27-Apr-15	19	0%					
SII11560	Sec II - MVB B: Excavation down to -9.5mPD	22-Apr-15	11-May-15	16	0%					
SII11580	Sec II - MVB B: Install Strut L4 at -8.5mPD	28-Apr-15	23-May-15	22	0%					
SII11600	Sec II - MVB B: Excavation down to -12.5mPD	14-May-15	30-May-15	14	0%					
SII11620	Sec II - MVB B: Install Strut L5 at -11.5mPD	19-May-15	12-Jun-15	21	0%					
MVB Substructure - Piling Works										
MVB C - Preboed H Piles										
SII10380	Sec II - MVB C - predrilling for preboared H-piles	02-May-15	30-May-15	24	0%					
MVB Substructure - Diaphragm Wall for Portion C										
MVB C - Dwall										
SII10620	Sec II - MVB C - Construct Guide Wall [P42-P43]	10-Mar-15	16-Mar-15	6	0%					
SII10622	Sec II - MVB C - construct Dwall [P42-P43] (1.5m thk on rock)	17-Mar-15	30-Apr-15	35	0%					

						CEDD Contract No. HK/2012/08 Wan Chai Development Phase II Central -Wan Chai Bypass at Wan Chai West					Page 2 / 4				
Activity ID	Activity Name	Early Start	Early Finish	Remaining Duration	Activity % Complete	2015									
							Mar	Apr	May	Jun					
Section II A - CWB Tunnel & Slip Road Structures and Facilities															
Section II A - CWB Tunnel - Design, Submission and Approval															
CWB Tunnel Temp Work Design for Structure															
SIIA10540	CWB Tunnel - Temp work design for tunnel structural works - prepare & submit to ICE	28-Feb-15	13-Apr-15	45	0%										
SIIA10560	CWB Tunnel - Temp work design for tunnel structural works - ICE check & issue check cert	14-Apr-15	09-May-15	26	0%										
SIIA10580	CWB Tunnel - Temp work design for tunnel structural works - Eng comment & approve	10-May-15	04-Jun-15	26	0%										
CWB CRIII & A1															
CWB CRIII & A1 - Dwall and Pile Construction															
SIIA10710	Sec II A - CWB CRIII - Construct pre-bored H-pile	22-Nov-14 A	07-Apr-15	32	5.88%										
SIIA10730	Sec II A - CWB CRIII - Loading Test	08-Apr-15	02-May-15	18	0%										
SIIA11140	Sec II A - CWB A1 - Construct pre-bored H-pile	31-Oct-14 A	31-Mar-15	27	53.45%										
CWB CRIII & A1 - Pumping Test Preparation/ Pumping Test															
CWB CRIII - Pumping Test Preparation															
SIIA10720	Sec II A - CWB CRIII - D-wall grout curtain / contact grout / fissure grout	01-Feb-15 A	30-Apr-15	49	0%										
SIIA10740	Sec II A - CWB CRIII - D-wall Sonic test / interface core	01-Feb-15 A	30-Apr-15	49	0%										
SIIA10760	Sec II A - CWB CRIII - install dewater/ recharge / observation well	02-May-15	26-May-15	20	0%										
CWB A1 - Pumping Testing Preparation															
SIIA11165	SIIA - CWB A1 - install shear pins to existing bored piles	16-Apr-15	16-May-15	26	0%										
SIIA11220	Sec II A - CWB A1 - D-wall Sonic test	28-Feb-15	15-Apr-15	36	0%										
SIIA11240	Sec II A - CWB A1 - install dewater/ recharge / observation well	27-May-15	18-Jun-15	20	0%										
CWB CRIII - ELS & Tunnel Structure															
CWB CRIII - ELS															
SIIA10820	Sec II A - CWB CRIII: Shoring & Excavation	20-Apr-15	31-Jul-15	85	0%										
CWB A1 - ELS & Tunnel Structure															
CWB A1 - ELS (Top-down Method) Roof															
SIIA11280	Sec II A - CWB A1: Shoring & Excavation (for Roof Slab)	24-Feb-15 A	14-Apr-15	35	12.5%										
CWB A1 - Tunnel Structure (Top down Method) Roof															
SIIA11300	Sec II A - CWB A1: Roof slab (1st Stage)	14-Apr-15	07-May-15	20	0%										
SIIA11440	Sec IIA - CWB A1 : Roof slab (2nd Stage)	17-Apr-15	11-May-15	20	0%										
SIIA13040	Sec II A - CWB A1: waterproofing and backfill before Culvert L construction	12-May-15	26-May-15	12	0%										
CWB A1 - ELS Remaining															
SIIA11286	Sec IIA - CWB A1 : Shoring & Excavation (Remaining)	27-May-15	31-Jul-15	55	0%										
CWB A1 - Other Works															
SIIA15480	Culvert L - [Summary] Bay 9 to Bay 11 on top of CWB A1 and divert flow	26-May-15	24-Jun-15	25	0%										
CWB B (& A2(1))															
CWB B - Dwall & Piling															
SIIA11520	Sec II A - CWB B (&A2(1)) : Construct Permanent DWall and barrette (1.2m thk on rock)	30-Oct-14 A	30-Apr-15	49	47.31%										
SIIA11525	Sec II A - CWB B (&A2(1)) : Construct temp Dwall (1.2m thk)	05-Nov-14 A	30-Apr-15	49	18.33%										
SIIA11540	Sec II A - CWB B (&A2(1)) : Construct pre-bored H-pile	20-Apr-15	14-Jul-15	70	0%										
SIIA11560	Sec II A - CWB B: Ground treatment to Stop End (MTR CWL)	16-May-15	30-Jul-15	62	0%										
CWB B - Pumping Test Preparation															
SIIA11580	Sec II A - CWB B: Dwall sonic test / interface core	25-Apr-15	08-Jul-15	60	0%										
SIIA11600	Sec II A - CWB B: Dwall precaution grout / fissure grout / grout curtain	25-Apr-15	08-Jul-15	60	0%										
CWB C (W)															
CWB C(W) - Dwall Construction															
SIIA11940	Sec II A - CWB CW: construct barrette	29-Dec-14 A	30-Apr-15	49	51%										
SIIA11945	Sec II A - CWB CW: construct Permanent DWall (1.5m thk) (on rock)	19-Jan-15 A	30-Apr-15	49	42.35%										
SIIA11960	Sec II A - CWB CW: Ground treatment to Stop End (MTR TWL)	16-May-15	30-Jul-15	62	0%										
SIIA11980	Sec II A - CWB CW: D-wall contact grout / fissure grout	27-Apr-15	27-Jul-15	75	0%										
SIIA12000	Sec II A - CWB CW: Dwall sonic test / interface core	27-Apr-15	27-Jul-15	75	0%										
CWB C (E)															

CEDD Contract No. HK/2012/08
Wan Chai Development Phase II
Central -Wan Chai Bypass at Wan Chai West

Activity ID	Activity Name	Early Start	Early Finish	Remaining Duration	Activity % Complete		Mar	2015 Apr	May	Jun
CWB C(E) & Enabling Work - Dwall Construction										
CWB C(E) - Dwall Construction										
SIIA12960	Sec II A - CWB CE: Predrilling for Dwall	18-Sep-14 A	14-May-15	60	33.33%					
SIIA12980	Sec II A - CWB CE: ground pre-treatment	30-Mar-15	19-Jun-15	65	0%					
SIIA13000	Sec II A - CWB CE: construct Guide Wall	04-Apr-15	02-Jun-15	45	0%					
SIIA13010	Sec II A - CWB CE: construct barrette (1.2m thk)	14-Apr-15	29-Sep-15	140	0%					
SIIA13020	Sec II A - CWB CE: construct Dwall (1.5m thk) (on rock)	14-Apr-15	19-Oct-15	156	0%					
SCL Enabling Work - Dwall Construction										
SIIA15520	Sec II - SCL Enabling Works - construct Dwall - Remaining [7 panels]	04-May-15	19-Oct-15	140	0%					
CWB D - Slip Road 1										
CWB D - Slip Road 1 - Dwall Construction & Piling										
SIIA12240	Sec II A - CWB SR1: Predrilling for Dwall & piles	15-Jan-15 A	27-May-15	70	22.22%					
SIIA12260	Sec II A - CWB SR1: ground pre-treatment	17-Jan-15 A	19-Jun-15	90	25%					
SIIA12280	Sec II A - CWB SR1: Guide Wall	10-Feb-15 A	03-Jul-15	100	0%					
SIIA12305	Sec II A - CWB SR1: construct Pemanent DWall (1.2m thk)	03-Apr-15	31-Jul-15	95	0%					
Section III - Road D11 & Part of Road P2, Area 4, Implement 1st Stage ITA										
Roadwork & Utilities										
General										
SIII10040	Sec III - roadwork & utilities - storm water drain & subsoil drain	28-Mar-15	22-Sep-15	145	0%					
SIII10060	Sec III - roadwork & utilities - Watermain & Irrigation Mains	23-Apr-15	02-Sep-15	110	0%					
SIII10080	Sec III - roadwork & utilities - gas main and valve chamber	16-May-15	24-Sep-15	110	0%					
Section VI A - Box Culvert La, L1 & FRP-L Construction										
Sec VI C - Box Culvert La bay 4 (North)										
CUL11645	Sec VI C - Culvert L - bay 4 (north half) - drive pipe pile	28-Feb-15	14-Apr-15	35	0%					
CUL11650	Sec VI C - Culvert L - bay 4 (north half) - demolish existing seawall	27-May-15	16-Jun-15	18	0%					
Box Culvert L1 & FRP-L Construction (Bay 5 - Bay 7)										
Box Culvert L1 & FRP-L - Bay 5 to 7 Piling										
CUL10800	Sec VI C - Culvert L - bay 7 (PC5 & PC6) - construct pre-bored H-pile	10-Mar-15*	29-Apr-15	40	0%					
CUL10820	Sec VI C - Culvert L - bay 6 (PC3 & PC4) - construct pre-bored H-pile	10-Feb-15 A	14-May-15	60	0%					
CUL10840	Sec VI C - Culvert L - bay 5 (PC1 & PC2) - construct pre-bored H-pile	10-Feb-15 A	25-Apr-15	45	0%					
CUL10940	Sec VI C - Culvert L - bay 5 (PC1 & PC2) - pile head treatment	14-Apr-15	13-May-15	30	0%					
CUL11020	Sec VI C - Culvert L - bay 6 (PC3 & PC4) - pile head treatment	14-May-15	28-May-15	15	0%					
CUL11025	Sec VI C - Culvert L - bay 7 (PC5 & PC6) - pile head treatment	29-May-15	12-Jun-15	15	0%					
Box Culvert L1 & FRP-L - Bay 5 to 7 Structure										
Box Culvert L1 & FRP-L - Precast Unit Fabrication (Pile Cap)										
CUL10866	Sec VI C - Culvert L - bay 5-7 - PC1 to PC5 Construct precast Pile Cap	29-Apr-15	18-Jun-15	42	0%					
Box Culvert L1 & FRP-L - Precast Unit Fabrication (Box Structure)										
CUL10868	Sec VI C - Culvert L - bay 5-7 - Fom Dry Dock for precast culvert units	15-Aug-14 A	07-Apr-15	32	56.76%					
CUL10870	Sec VI C - Culvert L - bay 5, 6 & 7 - Construct precast culvert units with Bulkhead	08-Apr-15	30-Jun-15	66	0%					
CUL10872	Sec VI C - Culvert L - bay 4b - Construct precast culvert units with Bulkhead	28-May-15	30-Jun-15	28	0%					
Box Culvert L1 & FRP-L - Precast Unit Installation										
CUL10864	Sec VI C - Culvert L - bay 5-7 - Demolition of Piling Platform	21-May-15	13-Jun-15	20	0%					
Box Culvert L1 & FRP-L - Bay 8										
Box Culvert L1 & FRP-L - Bay 8 Piling										
CUL10180	Culvert L - bay 8 - construct pre-bored H-pile	02-Apr-15	05-May-15	24	0%					
Box Culvert L1 & FRP-L - Bay 8 Temp Work & ELS										
CUL10190	Culvert L - Bay 8 - install sheetpile	06-May-15	21-May-15	14	0%					
CUL10200	Culvert L - bay 8 - ELS and bulk excavation & Dwall Break Through ready for Flow Diversion	22-May-15	30-May-15	7	0%					
Box Culvert L1 & FRP-L - Bay 9 to 11										
Box Culvert L1 & FRP-L - Bay 9 to 11 General										

Activity ID	Activity Name	Early Start	Early Finish	Remaining Duration	Activity % Complete		Mar	2015 Apr	May	Jun
CUL11690	CWB A1 - [Summary] Tunnel waterproofing and backfill for Culvert L construction	24-Feb-15 A	26-May-15	69	32.35%					
CUL11695	Culvert L - [Summary of Cul L bay 9 to 11] - construct in-situ box culverts	26-May-15	22-Jun-15	23	0%					
Box Culvert L1 & FRP-L - Bay 9										
CUL11700	Culvert L - bay 9 - construct base slab	26-May-15	30-May-15	5	0%					
Box Culvert L1 & FRP-L - Bay 10										
CUL11820	Culvert L - bay 10 - construct base slab	30-May-15	04-Jun-15	5	0%					
Box Culvert L1 & FRP-L - Bay 11										
CUL11880	Culvert L - bay 11 - construct base slab	28-May-15	02-Jun-15	5	0%					
Box Culvert L1 & FRP-L - Bay 12 to 13										
Box Culvert L1 & FRP-L - Bay 12 to 13 Piling										
CUL12354	Culvert L - bay 12 - construct pre-bored H-pile (PC9)	18-Apr-15	05-May-15	14	0%					
CUL12356	Culvert L - bay 13 - construct pre-bored H-pile (PC10 & PC11)	06-May-15	01-Jun-15	22	0%					
Box Culvert L1 & FRP-L - Bay 12 to 13 Temp Work & ELS										
CUL12365	Culvert L - Bay 12 - install sheetpile	06-May-15	21-May-15	14	0%					
CUL12385	Culvert L - bay 12 - ELS and bulk excavation	22-May-15	30-May-15	7	0%					
Section VI C - Area 3, 6, 8A & 8C										
Area 8A & 8C - Seawall Modification										
Modification of Seawall										
Modification of Seawall - Zone 1										
PRS10000	Sec VIC - Erection of Piling Platform	12-Mar-15*	04-Apr-15	21	0%					
PRS10020	Sec VIC - Piling Rig Mobilisation & Set up	07-Apr-15	17-Apr-15	7	0%					
PRS10040	Sec VIC - Pipe Pile (1st Stage - Approx. 5 nos.) With Grouting	18-Apr-15	08-May-15	17	0%					
Modification of Seawall - Zone 2 & 4										
PRS10120	Sec VIC - Piling Rig Mobilisation & Set Up (Zone 2)	09-May-15	16-May-15	7	0%					
PRS10140	Sec VIC - Pipe Pile (28 nos.) With Grouting (Zone 2)	18-May-15	29-Jul-15	60	0%					
Modification of Seawall - Zone 3										
PRS10200	Sec VIC - Removal of Platform of Bored Pile	09-May-15	16-May-15	7	0%					
PRS10220	Sec VIC - Excavation of Fluid & Rockfill	18-May-15	08-Jun-15	18	0%					
Area 6 - Box Culvert bay 5-6										
SVIC10000	Sec VI C - [Summary] Construct Box Culvert Bay 5-6	08-Apr-15	03-Aug-15	94	0%					
Area 3 - Box Culvert bay 4 and Roadwork										
SVIC10220	Sec VI C - [Summary] Construct Box Culvert Bay 4 in Area 3	01-Jan-15 A	13-Aug-15	135	0%					
Section VII - Remainder Works										
Tenders for Sub-contract and Material Procurement										
PCU70010	Sec VII - Prepare Sub-contract for removing interim landing steps	28-Mar-15	11-May-15	45	0%					
Landing Steps Construction										
SVII11180	Sec VII - Landing Steps - form temporary access from landing steps to Fleet Acade	09-May-15	01-Jun-15	18	0%					
Section VIII - Landscape Softworks										
Soft Landscaping Works										
SVIII10020	Sec VIII - Tree Felling/Transplanting at Portion 2 & 2A	20-Nov-13 A	06-Jun-15	79	12.22%					
Section X - Protection & Preservation of Trees										
Soft Landscaping Works										
SX10020	Sec X - Protection & Preservation of Trees	31-Jan-13 A	21-Jul-17	875	46.38%					



Activity ID	Activity Name	OD	RD	Start	Finish	Total Float	Calendar	2014	2015				
									Jan 61	Feb 62	Mar 63	Apr 64	May 65
Wan Chai Development Phase II - Central - Wan Chai Bypass at Wan Chai East (dd 20-Jan-14)		1909	469	24-Feb-10 18:00 A	29-Aug-16 18:00	640							
Programme Milestones (Revised up to EOTO No.10 Issued on 29-Nov-13)		106	106	20-Jan-15 18:00	07-May-15 08:00	-28	Calendar Day						
Contractual Completion Dates		21	21	20-Jan-15 18:00	10-Feb-15 18:00	0	Calendar Day						
KDC0110	Section 7 Works (831 days) - Box Culvert N1 & Works at Area 7 (7-May-12)	0	0		20-Jan-15 18:00*	-988	Calendar Day						
Soft Landscaping & Establishment Key Dates		21	21	20-Jan-15 18:00	10-Feb-15 18:00	0	Calendar Day						
KDC0140	Section 8C Works (1473 days) - Landscape Softworks in Area 8 (10-Feb-14)	0	0		20-Jan-15 18:00*	-344	Calendar Day						
KDC0150	Section 8D Works (1838 days) - Establishment Works in Area 8 (10-Feb-15)	0	0		10-Feb-15 18:00*	0	Calendar Day						
Forecast Completion Dates		4	4	07-Apr-15 18:00	11-Apr-15 18:00	-425	Calendar Day						
KDF0110	Section 7 Works (831 days) - Box Culvert N1 & Works at Area 7	0	0		11-Apr-15 18:00	-1069	Calendar Day						
Soft Landscaping & Establishment Key Dates		0	0	07-Apr-15 18:00	07-Apr-15 18:00	-421	Calendar Day						
KDF0140	Section 8C Works (1473 days) - Landscape Softworks in Area 8	0	0		07-Apr-15 18:00	-421	Calendar Day						
Possession of Site		0	0	07-May-15 08:00	07-May-15 08:00	-28	Calendar Day						
PS0090	Possession of Portion 9 - Western Bulkhead (By HK/2009/01)	0	0	07-May-15 08:00*		-28	Calendar Day						
Preliminaries		700	120	08-Jun-13 08:00 A	20-May-15 18:00	1264	Calendar Day						
Interface with Others		0	0	31-Mar-15 18:00	31-Mar-15 18:00	-308	Calendar Day						
PRE0950	Permanent Diversion of Box Culvert M by HK/2009/01	0	0		31-Mar-15 18:00*	-308	Calendar Day						
Critical Submission & Approval		700	120	08-Jun-13 08:00 A	20-May-15 18:00	1264	Calendar Day						
PRE-SUB-1000B	Temp Covered Walkway Capping Beam - Design Approval	30	7	19-Jun-13 08:00 A	27-Jan-15 18:00	1377	Calendar Day						
PRE-SUB-1010B	Temp Covered Walkway Cover System (PS30.5) - Design Approval	30	7	12-Jun-14 08:00 A	27-Jan-15 18:00	1377	Calendar Day						
CSD for CWB Tunnel		700	120	08-Jun-13 08:00 A	20-May-15 18:00	1264	Calendar Day						
PRE-CSD-2030B	Tunnel Portion 2 - Redesigned CWB Tunnel Structure Design Submission Approval by AECOM	60	30	16-Nov-13 08:00 A	19-Feb-15 18:00	-63	Calendar Day						
PRE-CSD-3000B	Tunnel Portion 3&4 - Redesigned Temp D-Wall Submission Approval by AECOM & GEO	30	10	08-Jun-13 08:00 A	30-Jan-15 18:00	1374	Calendar Day						
PRE-CSD-3010B	Tunnel Portion 3&4 - ELS Submission Approval by AECOM & GEO	60	30	17-Jan-14 08:00 A	19-Feb-15 18:00	-352	Calendar Day						
PRE-CSD-5000B	Tunnel Portion 5 - Temp D-Wall Submission Approval by AECOM & GEO	60	30	15-Aug-13 08:00 A	19-Feb-15 18:00	-252	Calendar Day						
PRE-CSD-5010A	Tunnel Portion 5 - ELS ICE Submission	120	120	21-Jan-15 08:00	20-May-15 18:00	-346	Calendar Day						
PRE-CSD-6010A	Tunnel Portion 6 - ELS ICE Submission	120	120	21-Jan-15 08:00	20-May-15 18:00	-33	Calendar Day						
Critical Procurement & Site Delivery		60	21	15-Jun-14 08:00 A	10-Feb-15 18:00	1363	Calendar Day						
PRE-PRO-1100B	GRP Roof Panel for Temp Covered Walkway (Type 2)	60	21	15-Jun-14 08:00 A	10-Feb-15 18:00	1363	Calendar Day						
Section 3 of the Works - Reprovisioning of Government Helipad and Public Toilet		254	25	11-Aug-12 08:00 A	18-Feb-15 18:00	1084	HK Working Day						
Outstanding Works		254	25	11-Aug-12 08:00 A	18-Feb-15 18:00	1084	HK Working Day						
S3-0070-1499	Reinstatement of armour rock, retaining walls & new covered walkway along Expo Drive East	254	25	11-Aug-12 08:00 A	18-Feb-15 18:00	1084	HK Working Day						
Section 4A of the Works - Cooling Water Pumping System for Sun Hung Kai Centre (P8)		365	73	16-Feb-14 08:00 A	03-Apr-15 18:00	1311	Calendar Day						
Cooling Mains Work above Tunnel Portion & connecting to Pump Station		365	73	16-Feb-14 08:00 A	03-Apr-15 18:00	1311	Calendar Day						
S4A-0900	Outstanding Works	365	73	16-Feb-14 08:00 A	03-Apr-15 18:00	1311	Calendar Day						
Section 4B of the Works - Cooling Water Pumping System for China Resources Building (P9)		365	7	01-Oct-13 08:00 A	27-Jan-15 18:00	1377	Calendar Day						
Cooling Mains Work above Tunnel Portion & connecting to Pump Station		365	7	01-Oct-13 08:00 A	27-Jan-15 18:00	1377	Calendar Day						
S4B-0900	Outstanding Works	365	7	01-Oct-13 08:00 A	27-Jan-15 18:00	1377	Calendar Day						
Section 4C of the Works - Cooling Water Pumping System for Great Eagle Centre / Harbour Centre (P7)		365	7	21-Nov-13 08:00 A	27-Jan-15 18:00	1377	Calendar Day						
Cooling Mains Work above Tunnel Portion & connecting to Pump Station		365	7	21-Nov-13 08:00 A	27-Jan-15 18:00	1377	Calendar Day						
S4C-0900	Outstanding Works	365	7	21-Nov-13 08:00 A	27-Jan-15 18:00	1377	Calendar Day						
Section 5 of the Works - WSD Salt Water Pumping System		365	73	06-Mar-14 08:00 A	03-Apr-15 18:00	1311	Calendar Day						
Overall Testing & Commissioning of Reprovisioned Salt Water Intake System		365	73	06-Mar-14 08:00 A	03-Apr-15 18:00	1311	Calendar Day						
S5-0900	Outstanding Works	365	73	06-Mar-14 08:00 A	03-Apr-15 18:00	1311	Calendar Day						
Section 7 of the Works - Box Culvert N1 & Flood Relief System		116	60	29-Oct-14 08:00 A	11-Apr-15 18:00	1049							
Transformer Building for Dining Services at Ferry Pier (VO116)		116	60	29-Oct-14 08:00 A	11-Apr-15 18:00	1049							
Civil Works		34	34	21-Jan-15 08:00	07-Mar-15 18:00	-833							
S7-TB-2065	Waterproof applicaion and testing for Roof Top Slab	6	6	21-Jan-15 08:00	26-Jan-15 18:00	-1022	Calendar Day						
S7-TB-2080	Formwork Removal & Scaffolding Dismantling	4	4	04-Mar-15 08:00	07-Mar-15 18:00	-833	HK Working Day						
ABWF Works		72	72	05-Jan-15 08:00 A	02-Apr-15 18:00	-695	Calendar Day						
S7-TB-3000	ABWF Works	60	42	05-Jan-15 08:00 A	03-Mar-15 18:00	-1035	Calendar Day						
S7-TB-3100	Landscaping Works	30	30	04-Mar-15 08:00	02-Apr-15 18:00	-695	Calendar Day						
E&M Works		151	67	29-Oct-14 08:00 A	28-Mar-15 18:00	1317	Calendar Day						
S7-TB-4000	E&M Installation (with individual testing)	30	30	18-Dec-14 08:00 A	19-Feb-15 18:00	-1069	Calendar Day						
S7-TB-4100	22kV Cable across HHR to Transformer Building by HEC	45	20	29-Oct-14 08:00 A	09-Feb-15 18:00	1364	Calendar Day						
S7-TB-4200	LV Cable Laying to Ferry Pier	30	29	02-Jan-15 08:00 A	18-Feb-15 13:30	-1068	Calendar Day						
S7-TB-4300	Transformer Installation by HEC	30	30	20-Feb-15 08:00	21-Mar-15 18:00	-1069	Calendar Day						
S7-TB-4400	Energization of Transformer	7	7	22-Mar-15 08:00	28-Mar-15 18:00	-1069	Calendar Day						
Overall Testing & Commissioning		51	51	20-Feb-15 08:00	11-Apr-15 18:00	-1069	Calendar Day						
S7-TB-9000	WSD Inspection & Water Cert Approval	14	14	20-Feb-15 08:00	05-Mar-15 18:00	-1046	Calendar Day						
S7-TB-9100	FSD Inspection & Fire Cert Approval	14	14	29-Mar-15 08:00	11-Apr-15 18:00	-1069	Calendar Day						
Section 8A of the Works - Reprovisioning of Wan Chai Ferry Pier in Area 8		212	36	10-Sep-13 08:00 A	25-Feb-15 18:00	1348	Calendar Day						
ABWF & E&M Installation		212	36	10-Sep-13 08:00 A	25-Feb-15 18:00	1348	Calendar Day						
Roof		212	36	10-Sep-13 08:00 A	25-Feb-15 18:00	1348	Calendar Day						
S8A-BS-4010	E&M Installation	28	10	10-Sep-13 08:00 A	30-Jan-15 18:00	1374	Calendar Day						
Works in Area 8 - ABWF Works at Observation Deck of Ferry Pier		120	36	28-Oct-13 08:00 A	25-Feb-15 18:00	1348	Calendar Day						
S8B-FP-01100	Roof Finishes & Misc. ABWF Installation	120	36	28-Oct-13 08:00 A	25-Feb-15 18:00	1348	Calendar Day						
S8B-FP-01300	Handrail & Glass Balustrade Installation	45	36	21-Dec-13 08:00 A	25-Feb-15 18:00	1348	Calendar Day						
Section 9B of the Works - CWB Tunnel Structure (CH3400 - CH3796)		427	301	20-Aug-14 08:00 A	05-Feb-16 17:43	-72							

Activity ID	Activity Name	OD	RD	Start	Finish	Total Float	Calendar	2014	2015				
									Jan	Feb	Mar	Apr	May
									61	62	63	64	65
Tunnel Portion 1 (CH3500-CH3630)													
CWB Structural Works													
Bay 6 (For OHVD Base Slab & Side Wall, Combined to Bay 5)													
Wall													
S9B-T1-B6-1120	Wall (Middle Late Cast) - Rebar Fixing	4	4	06-Feb-15 08:00	10-Feb-15 18:00	205	HK Working Day						
S9B-T1-B6-1130A	Wall (Middle Late Cast) - Formwork	3	3	11-Feb-15 08:00	13-Feb-15 18:00	205	HK Working Day						
S9B-T1-B6-1130B	Wall (Middle Late Cast) - Concrete	1	1	14-Feb-15 08:00	14-Feb-15 18:00	205	HK Working Day						
S9B-T1-B6-1140	Wall (Middle Late Cast) - Curing & Formwork Removal	3	3	15-Feb-15 08:00	17-Feb-15 18:00	259	Calendar Day						
Tunnel Portion 2 (CH3425-CH3500)													
CWB Structural Works													
S9B-T2-2000	Tunnel portion 2 ELSW excavation (62,500m3; 500m3/d)	125	13	20-Aug-14 08:00 A	04-Feb-15 13:30	11	HK Working Day						
S9B-T2-3000	Tunnel Portion 2 - Trim Bored Pile Head, Blinding	21	20	19-Jan-15 08:00 A	12-Feb-15 17:33	-31	HK Working Day						
S9B-T2-4000	Strut S5 Removal	7	7	28-Apr-15 08:00	06-May-15 18:00	-50	HK Working Day						
S9B-T2-4200	Bulk Head Demolition between TP1 & TP2 @ CH3500 & Baseslab Stitching	14	14	16-Jan-15 08:00 A	05-Feb-15 18:00	19	HK Working Day						
Bay 1													
S9B-T2-B1-1010	Base Slab - Waterproofing	4	4	26-Feb-15 08:00	02-Mar-15 18:00	-50	HK Working Day						
S9B-T2-B1-1020	Base Slab - Formwork & Rebar Fixing	14	14	03-Mar-15 08:00	18-Mar-15 18:00	-38	HK Working Day						
S9B-T2-B1-1030	Base Slab - Concrete & Curing	5	5	19-Mar-15 08:00	23-Mar-15 18:00	-35	Calendar Day						
Bay 2													
S9B-T2-B2-1010	Base Slab - Waterproofing	4	4	03-Mar-15 08:00	06-Mar-15 18:00	-50	HK Working Day						
S9B-T2-B2-1020	Base Slab - Formwork & Rebar Fixing	14	14	07-Mar-15 08:00	23-Mar-15 18:00	-28	HK Working Day						
S9B-T2-B2-1030	Base Slab - Concrete & Curing	5	5	24-Mar-15 08:00	28-Mar-15 18:00	-40	Calendar Day						
Bay 3													
S9B-T2-B3-1010	Base Slab - Waterproofing	4	4	07-Mar-15 08:00	11-Mar-15 18:00	-50	HK Working Day						
S9B-T2-B3-1020	Base Slab - Formwork & Rebar Fixing	14	14	19-Mar-15 08:00	08-Apr-15 18:00	-38	HK Working Day						
S9B-T2-B3-1030	Base Slab - Concrete & Curing	5	5	09-Apr-15 08:00	13-Apr-15 18:00	-56	Calendar Day						
S9B-T2-B3-3000	Wall (South) - Waterproofing	4	4	16-May-15 08:00	20-May-15 18:00	-50	HK Working Day						
S9B-T2-B3-3010	Wall (Middle) - Rebar Fixing	4	4	16-May-15 08:00	20-May-15 18:00	-47	HK Working Day						
S9B-T2-B3-3020	Wall (North) - Waterproofing	4	4	16-May-15 08:00	20-May-15 18:00	-50	HK Working Day						
Bay 4													
S9B-T2-B4-1010	Base Slab - Waterproofing	4	4	12-Mar-15 08:00	16-Mar-15 18:00	-50	HK Working Day						
S9B-T2-B4-1020	Base Slab - Formwork & Rebar Fixing	14	14	17-Mar-15 08:00	01-Apr-15 18:00	-50	HK Working Day						
S9B-T2-B4-1030	Base Slab - Concrete & Curing	5	5	02-Apr-15 08:00	06-Apr-15 18:00	-49	Calendar Day						
S9B-T2-B4-3000	Wall (South) - Waterproofing	4	4	12-May-15 08:00	15-May-15 18:00	-50	HK Working Day						
S9B-T2-B4-3010	Wall (Middle) - Rebar Fixing	4	4	12-May-15 08:00	15-May-15 18:00	-47	HK Working Day						
S9B-T2-B4-3020	Wall (North) - Waterproofing	4	4	12-May-15 08:00	15-May-15 18:00	-50	HK Working Day						
S9B-T2-B4-3030	Wall (South) - Rebar Fixing	3	3	16-May-15 08:00	19-May-15 18:00	-38	HK Working Day						
S9B-T2-B4-3040	Wall (North) - Rebar Fixing	3	3	16-May-15 08:00	19-May-15 18:00	-38	HK Working Day						
S9B-T2-B4-3050	Wall (Middle) - Formwork & Concrete	3	3	16-May-15 08:00	19-May-15 18:00	-35	HK Working Day						
Bay 5													
S9B-T2-B5-1010	Base Slab - Waterproofing	4	4	17-Mar-15 08:00	20-Mar-15 18:00	-40	HK Working Day						
S9B-T2-B5-1020	Base Slab - Formwork & Rebar Fixing	14	14	02-Apr-15 08:00	22-Apr-15 18:00	-50	HK Working Day						
S9B-T2-B5-1030	Base Slab - Concrete & Curing	5	5	23-Apr-15 08:00	27-Apr-15 18:00	-70	Calendar Day						
S9B-T2-B5-3000	Wall (South) - Waterproofing	4	4	07-May-15 08:00	11-May-15 18:00	-50	HK Working Day						
S9B-T2-B5-3010	Wall (Middle) - Rebar Fixing	4	4	07-May-15 08:00	11-May-15 18:00	-47	HK Working Day						
S9B-T2-B5-3020	Wall (North) - Waterproofing	4	4	07-May-15 08:00	11-May-15 18:00	-50	HK Working Day						
S9B-T2-B5-3030	Wall (South) - Rebar Fixing	3	3	12-May-15 08:00	14-May-15 18:00	-34	HK Working Day						
S9B-T2-B5-3040	Wall (North) - Rebar Fixing	3	3	12-May-15 08:00	14-May-15 18:00	-34	HK Working Day						
S9B-T2-B5-3050	Wall (Middle) - Formwork & Concrete	3	3	12-May-15 08:00	14-May-15 18:00	-31	HK Working Day						
S9B-T2-B5-3060	Wall (South) - Formwork & Concrete	3	3	15-May-15 08:00	18-May-15 18:00	-34	HK Working Day						
S9B-T2-B5-3070	Wall (North) - Formwork & Concrete	3	3	15-May-15 08:00	18-May-15 18:00	-34	HK Working Day						
S9B-T2-B5-3080	Wall (Middle) - Curing & Formwork Removal	3	3	15-May-15 08:00	17-May-15 18:00	-40	Calendar Day						
S9B-T2-B5-3090	Wall (South) - Curing & Formwork Removal	3	3	19-May-15 08:00	21-May-15 18:00	-44	Calendar Day						
S9B-T2-B5-3100	Wall (North) - Curing & Formwork Removal	3	3	19-May-15 08:00	21-May-15 18:00	-44	Calendar Day						
Tunnel Portion 3 & Tunnel Portion 4 (CH3630-CH3790)													
Foundation													
Stage 3 - Northern Wall after TWCR4 Reclamation (C88-C105)													
S9B-T34-1430C	D-wall Construction at TWCR4 (C88-P94; P101-C105; 6d/Panel)	84	13	31-Oct-14 08:00 A	02-Feb-15 14:24	-349	Calendar Day						
Stage 4 - Southern Wall after HHR Flyover Diversion (Stage 2) (P132-P143)													
S9B-T34-1640	D-wall Construction at Original HHR Flyover Approach Ramp (P132-P143; 8d/Panel)	96	80	08-Jan-15 08:00 A	10-Apr-15 17:43	-416	Calendar Day						
S9B-T34-1660	Capping Beam Construction Between Tunnel Portion 1 and 3 & 4	14	13	21-Jan-15 14:24 A	03-Feb-15 10:42	-335	Calendar Day						
S9B-T34-1670	Installation of Pump Well, Observation Well, Inclinator and Piezometers	28	22	08-Jan-15 14:24 A	12-Feb-15 11:36	-358	Calendar Day						
S9B-T34-1700	Tunnel Portion 3 & 4 Pumping test	28	28	10-Apr-15 17:43	08-May-15 17:43	-416	Calendar Day						
CWB Structural Works													
S9B-T34-2000	Tunnel Portion 3 & 4 Excavation (198,000m3 soil @1500m3/d; 2000m3 rock @100m3/d) & ELS	230	230	24-Apr-15 17:43	05-Feb-16 17:43	-333	HK Working Day						
Section 10 Works - CWB Tunnel Structure (CH3246 - CH3400)													
Tunnel Portion 6 (CH3246-CH3280)													
S10-T6-1020	Tunnel Portion 6 Bored Pile - 13nr. (3 sets @ 12d/pile)	52	52	07-May-15 08:00	09-Jul-15 18:00	-23	HK Working Day						
Section 11 of the Works - Remainder of Works													

Activity ID	Activity Name	OD	RD	Start	Finish	Total Float	Calendar	2014	2015				
									Jan	Feb	Mar	Apr	May
									61	62	63	64	65
Marine Works at WCR3		184	123	05-Dec-14 08:00 A	23-May-15 18:00	-486	Calendar Day						
S11-R3-0500	Fabrication of Caisson Seawalls for WCR3 Reclamation (1st Stage - 5 Nos.)	60	30	05-Dec-14 08:00 A	19-Feb-15 18:00	-466	Calendar Day						
S11-R3-1300	1st Stage Rockfilling for Seawall (24,000m3 @ 1000m3/d)	24	12	22-Dec-14 08:00 A	01-Feb-15 18:00	-486	Calendar Day						
S11-R3-1400	Placing leveling stones to -6.0mPD (1500m2 @ 40m2/d)	38	38	02-Feb-15 08:00	11-Mar-15 18:00	-486	Calendar Day						
S11-R3-1500	Installation of Permanent Seawall (5 nos.) & Rockfilling behind seawall	16	16	12-Mar-15 08:00	27-Mar-15 18:00	-486	Calendar Day						
S11-R3-1600	2nd Stage Dredging incl. Existing Wan Chai Ferry Pier (20,000m3 @ 1,000m3/d)	20	17	15-Jan-15 08:00 A	06-Feb-15 18:00	-437	Calendar Day						
S11-R3-1700	Reclamation from -14 mPD to -2.0mPD by Hopper (121,000m3 @ 3,000m3/d)	41	41	28-Mar-15 08:00	07-May-15 18:00	-486	Calendar Day						
S11-R3-1800	Installation of Permanent Seawall & Rockfilling behind seawall	16	16	08-May-15 08:00	23-May-15 18:00	-486	Calendar Day						
Soft Landscaping & Establishment Works		2375	587	24-Feb-10 18:00 A	29-Aug-16 18:00	0	Calendar Day						
Section 8C of the Works - Landscape Softworks in Area 8		90	77	07-Oct-14 08:00 A	07-Apr-15 18:00	-421	Calendar Day						
S8C-0010	Carry out landscape soft work on new ferry pier	90	77	07-Oct-14 08:00 A	07-Apr-15 18:00	-421	Calendar Day						
Section 8D of the Works - Establishment Works in Area 8		365	365	08-Apr-15 08:00	06-Apr-16 18:00	-421	Calendar Day						
S8D-0010	Carry out establishment work on new ferry pier	365	365	08-Apr-15 08:00	06-Apr-16 18:00	-421	Calendar Day						
Section 12 of the Works - Protection and Preservation of Existing Trees		2375	587	24-Feb-10 18:00 A	29-Aug-16 18:00	0	Calendar Day						
S12-0010	Protection and preservation of existing trees	2375	587	24-Feb-10 18:00 A	29-Aug-16 18:00	0	Calendar Day						
SUMMARY PROGRAMME		992	381	07-May-13 08:00 A	05-Feb-16 17:43	1003	Calendar Day						
CWB Tunnel Construction & Remaining Works (Section 9A, 9B, 10 & 11)		795	381	11-Nov-13 08:00 A	05-Feb-16 17:43	-158	Calendar Day						
CWB Tunnel Works in WCR2		396	285	17-Oct-14 08:00 A	01-Nov-15 18:00	-62	Calendar Day						
SUM-CWB-22000	Pump Test & Excavation for Tunnel Portion 2	134	15	17-Oct-14 08:00 A	04-Feb-15 13:30	13	Calendar Day						
SUM-CWB-23000	CWB Tunnel Portion 2 Construction	261	285	19-Jan-15 08:00 A	01-Nov-15 18:00	-62	Calendar Day						
CWB Tunnel Works in WCR3		314	170	30-Aug-14 08:00 A	09-Jul-15 18:00	-29	Calendar Day						
SUM-CWB-30000	Reclamation at WCR3 & Ferry Pier Demolition (Except Water Channel Maintained for HK/2009/	209	158	30-Aug-14 08:00 A	27-Jun-15 18:00	-486	Calendar Day						
SUM-CWB-35000B	Foundation for Tunnel Portion 6 - Bored Pile	64	64	07-May-15 08:00	09-Jul-15 18:00	-29	Calendar Day						
CWB Tunnel Works in WCR4/TWCR4		795	381	11-Nov-13 08:00 A	05-Feb-16 17:43	-368	Calendar Day						
SUM-CWB-41000B	Foundation for Tunnel Portion 3&4 (except Eastern Bulkhead Wall)	457	80	11-Nov-13 08:00 A	10-Apr-15 17:43	-67	Calendar Day						
SUM-CWB-42000	Pump Test & Excavation for Tunnel Portion 3&4	301	301	10-Apr-15 17:43	05-Feb-16 17:43	-422	Calendar Day						
Reprovisioning of Existing Facilities (Section 3, 4A, 4B, 4C, 5, 6, 7, 8A & 8B)		754	81	07-May-13 08:00 A	11-Apr-15 18:00	1303	Calendar Day						
Reprovisioning of Box Culvert N (Section 7)		249	81	08-Oct-14 00:00 A	11-Apr-15 18:00	-1069	Calendar Day						
SUM-FAC-52000	VO116 - New Transformer Building to Ferry Pier	249	81	08-Oct-14 00:00 A	11-Apr-15 18:00	-1069	Calendar Day						
Reprovisioning of Wan Chai Ferry Pier & Covered Walkway (Section 8A & 8B)		150	36	07-May-13 08:00 A	25-Feb-15 18:00	1348	Calendar Day						
SUM-FAC-65000	ABWF Works on Observation Deck under Section 8B	150	36	07-May-13 08:00 A	25-Feb-15 18:00	1348	Calendar Day						

CEDD CONTRACT HK/2009/02

CHUN WO - CRGL JOINT VENTURE

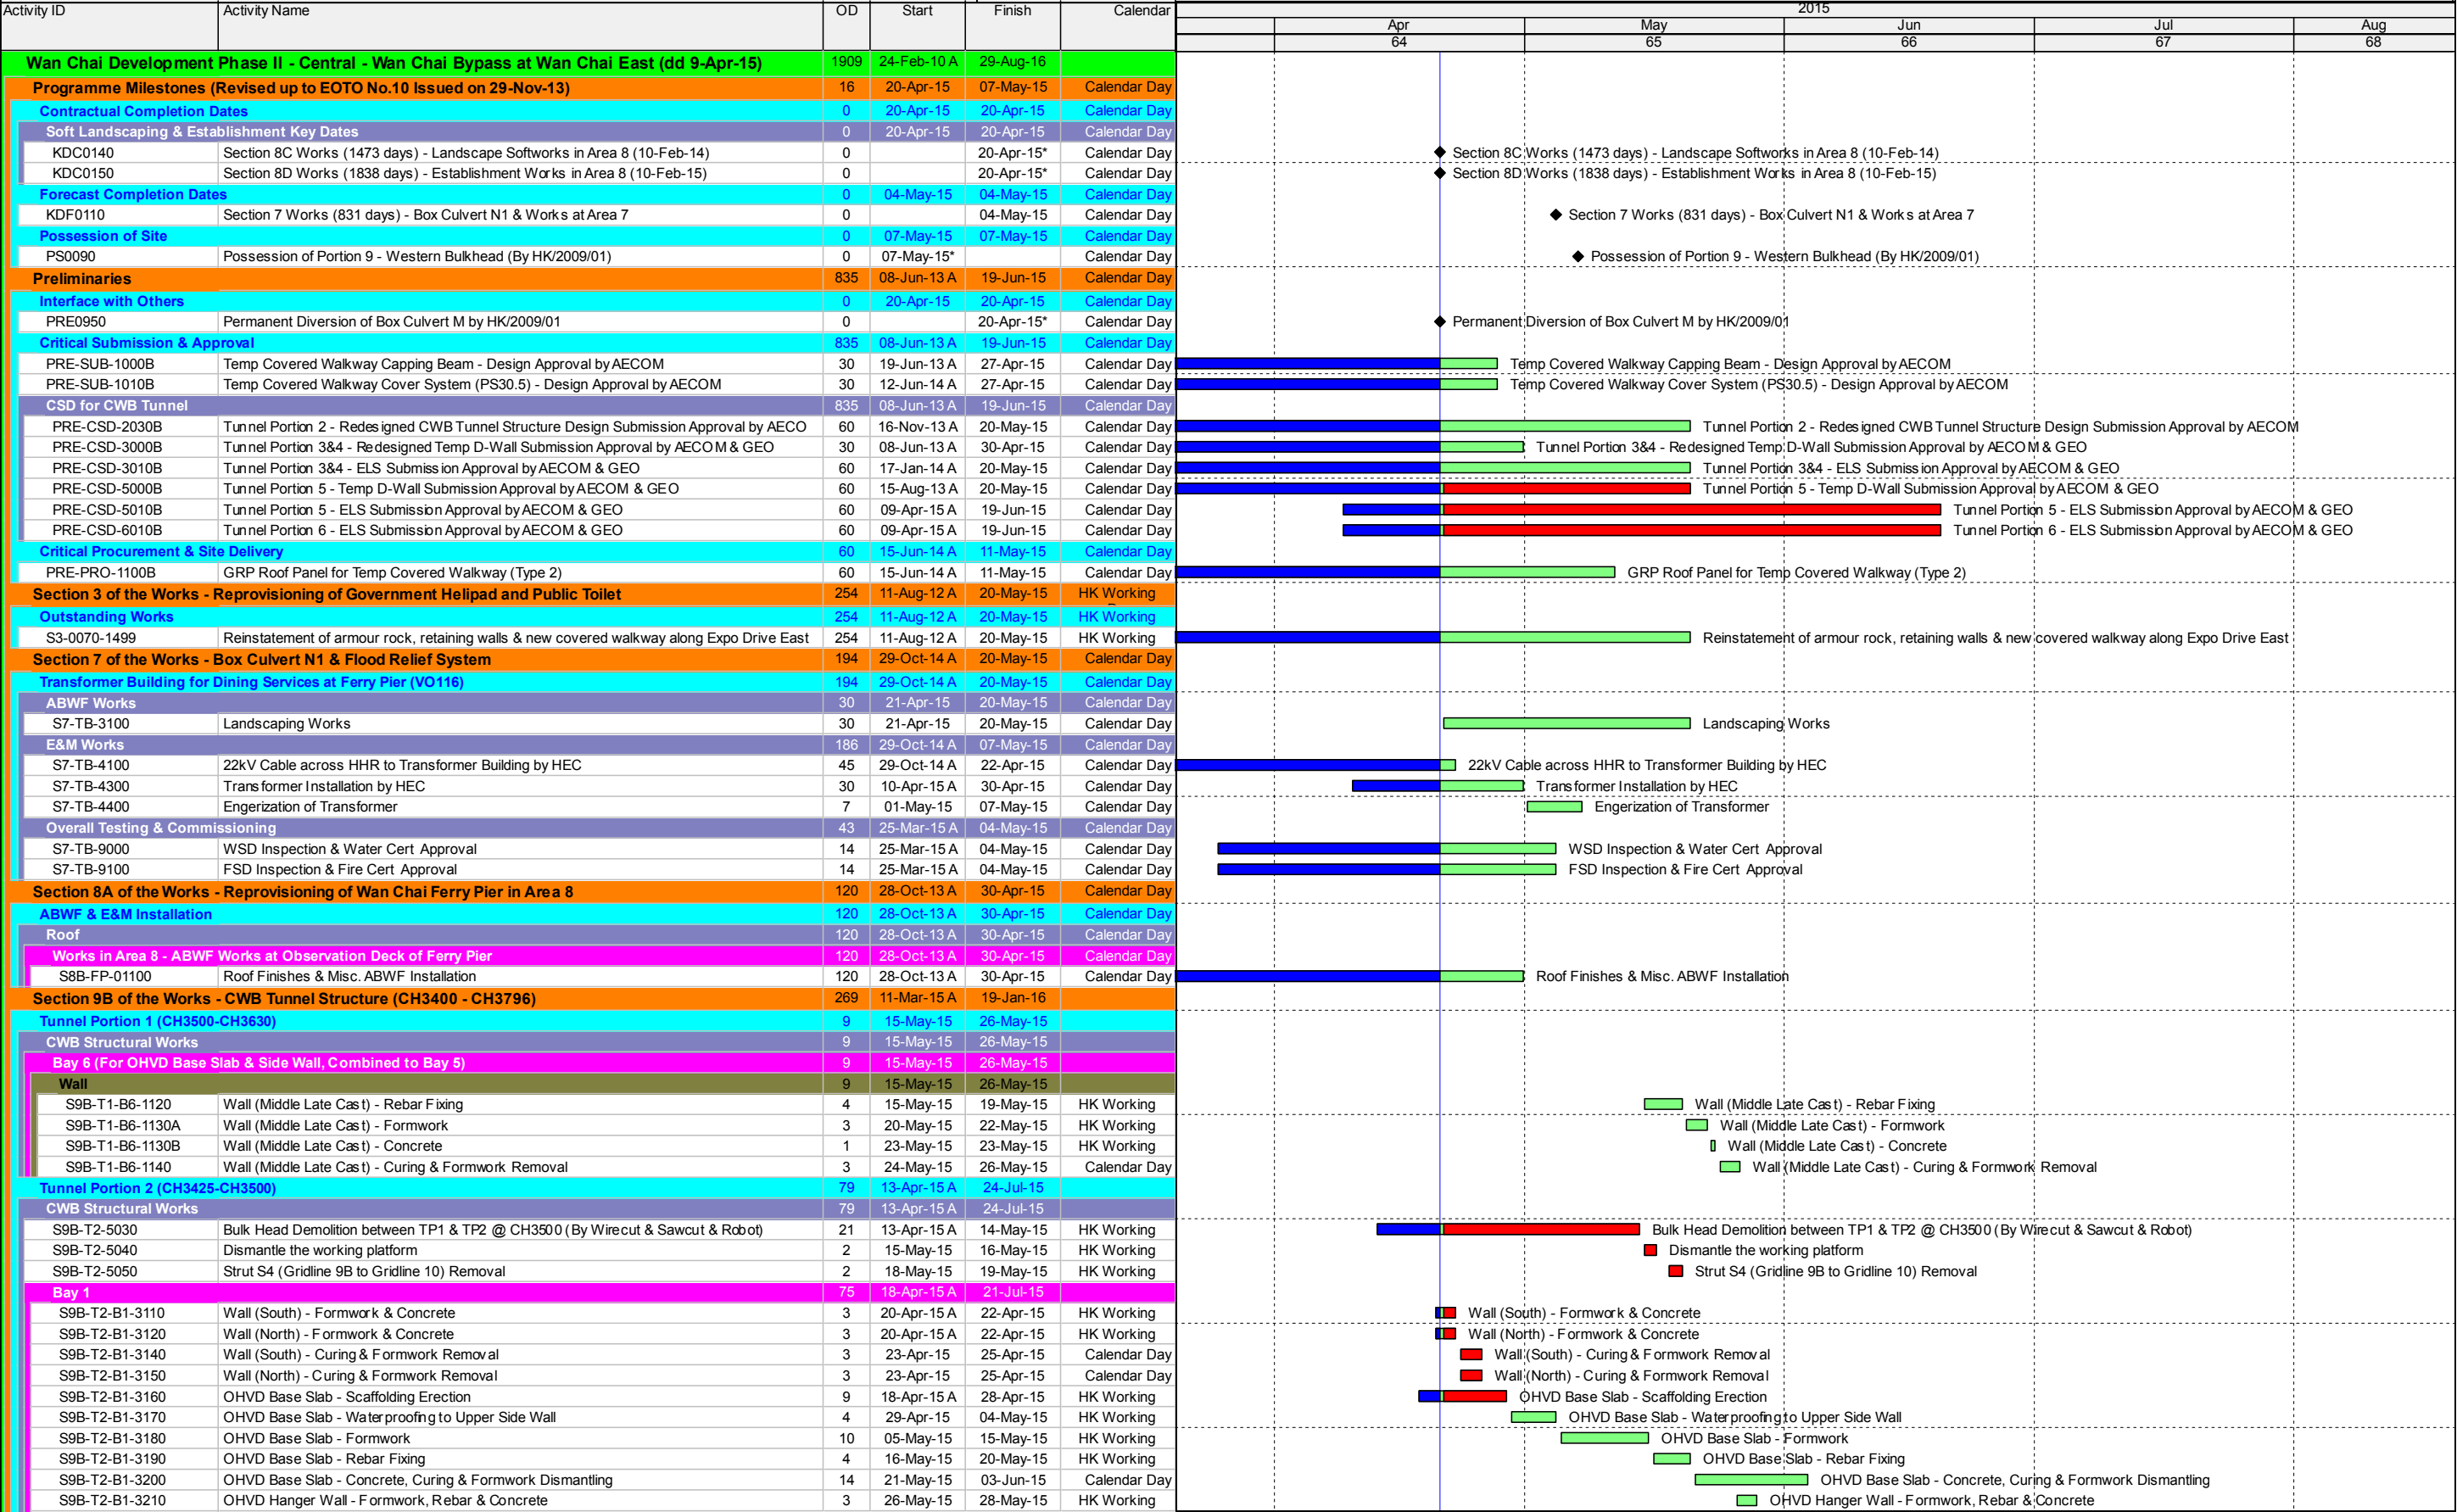

- Remaining Work
- Actual Work
- Summary Bar
- Critical Remaining Work
- Milestone

CEDD CONTRACT NO. HK/2009/02
Wan Chai Development Phase II - Central-Wan Chai Bypass at Wan Chai East (Contract 2)
3-MONTH ROLLING PROGRAMME (dd 20-Apr-15)

Date	Revision	Checked	Approved
20-Apr-15	3MRP		
20-Sep-14	Revised WP		

Page 1 of 3
TASK filter: 3-Month Rolling.
Print on: 23-Apr-15 09:36

Activity ID	Activity Name	OD	Start	Finish	Calendar	2015					
						Apr	May	Jun	Jul	Aug	
						64	65	66	67	68	
S9B-T2-B1-3220	Roof - Scaffolding Erection for Roof	7	04-Jun-15	11-Jun-15	HK Working			Roof - Scaffolding Erection for Roof			
S9B-T2-B1-3230	Roof - Formwork	9	12-Jun-15	23-Jun-15	HK Working			Roof - Formwork			
S9B-T2-B1-3240	Roof - Rebar Fixing	10	24-Jun-15	06-Jul-15	HK Working			Roof - Rebar Fixing			
S9B-T2-B1-3250	Roof - Concrete & Curing	15	07-Jul-15	21-Jul-15	Calendar Day			Roof - Concrete & Curing			
Bay 2						70	27-Apr-15	21-Jul-15			
S9B-T2-B2-3060	Wall (South) - Formwork & Concrete	3	27-Apr-15	29-Apr-15	HK Working		Wall (South) - Formwork & Concrete				
S9B-T2-B2-3070	Wall (North) - Formwork & Concrete	3	27-Apr-15	29-Apr-15	HK Working		Wall (North) - Formwork & Concrete				
S9B-T2-B2-3090	Wall (South) - Curing & Formwork Removal	3	30-Apr-15	02-May-15	Calendar Day		Wall (South) - Curing & Formwork Removal				
S9B-T2-B2-3100	Wall (North) - Curing & Formwork Removal	3	30-Apr-15	02-May-15	Calendar Day		Wall (North) - Curing & Formwork Removal				
S9B-T2-B2-3110	OHVD Base Slab - Scaffolding Erection	9	04-May-15	13-May-15	HK Working		OHVD Base Slab - Scaffolding Erection				
S9B-T2-B2-3120	OHVD Base Slab - Waterproofing to Upper Side Wall	4	14-May-15	18-May-15	HK Working		OHVD Base Slab - Waterproofing to Upper Side Wall				
S9B-T2-B2-3130	OHVD Base Slab - Formwork	10	19-May-15	30-May-15	HK Working		OHVD Base Slab - Formwork				
S9B-T2-B2-3140	OHVD Base Slab - Rebar Fixing	4	01-Jun-15	04-Jun-15	HK Working		OHVD Base Slab - Rebar Fixing				
S9B-T2-B2-3150	OHVD Base Slab - Concrete, Curing & Formwork Dismantling	14	05-Jun-15	18-Jun-15	Calendar Day		OHVD Base Slab - Concrete, Curing & Formwork Dismantling				
S9B-T2-B2-3160	OHVD Hanger Wall - Formwork, Rebar & Concrete	3	08-Jun-15	10-Jun-15	HK Working		OHVD Hanger Wall - Formwork, Rebar & Concrete				
S9B-T2-B2-3170	Roof - Scaffolding Erection for Roof	7	19-Jun-15	27-Jun-15	HK Working		Roof - Scaffolding Erection for Roof				
S9B-T2-B2-3180	Roof - Formwork	9	29-Jun-15	09-Jul-15	HK Working		Roof - Formwork				
S9B-T2-B2-3190	Roof - Rebar Fixing	10	10-Jul-15	21-Jul-15	HK Working		Roof - Rebar Fixing				
Bay 3						67	20-Apr-15 A	18-Jul-15			
S9B-T2-B3-3060	Wall (South) - Formwork & Concrete	3	04-May-15	06-May-15	HK Working		Wall (South) - Formwork & Concrete				
S9B-T2-B3-3070	Wall (North) - Formwork & Concrete	3	04-May-15	06-May-15	HK Working		Wall (North) - Formwork & Concrete				
S9B-T2-B3-3080	Wall (Middle) - Curing & Formwork Removal	3	20-Apr-15 A	22-Apr-15	Calendar Day		Wall (Middle) - Curing & Formwork Removal				
S9B-T2-B3-3090	Wall (South) - Curing & Formwork Removal	3	07-May-15	09-May-15	Calendar Day		Wall (South) - Curing & Formwork Removal				
S9B-T2-B3-3100	Wall (North) - Curing & Formwork Removal	3	07-May-15	09-May-15	Calendar Day		Wall (North) - Curing & Formwork Removal				
S9B-T2-B3-3110	OHVD Base Slab - Scaffolding Erection	9	14-May-15	23-May-15	HK Working		OHVD Base Slab - Scaffolding Erection				
S9B-T2-B3-3120	OHVD Base Slab - Waterproofing to Upper Side Wall	4	26-May-15	29-May-15	HK Working		OHVD Base Slab - Waterproofing to Upper Side Wall				
S9B-T2-B3-3130	OHVD Base Slab - Formwork	10	30-May-15	10-Jun-15	HK Working		OHVD Base Slab - Formwork				
S9B-T2-B3-3140	OHVD Base Slab - Rebar Fixing	4	11-Jun-15	15-Jun-15	HK Working		OHVD Base Slab - Rebar Fixing				
S9B-T2-B3-3150	OHVD Base Slab - Concrete, Curing & Formwork Dismantling	14	16-Jun-15	29-Jun-15	Calendar Day		OHVD Base Slab - Concrete, Curing & Formwork Dismantling				
S9B-T2-B3-3160	OHVD Hanger Wall - Formwork, Rebar & Concrete	3	19-Jun-15	23-Jun-15	HK Working		OHVD Hanger Wall - Formwork, Rebar & Concrete				
S9B-T2-B3-3170	Roof - Scaffolding Erection for Roof	7	30-Jun-15	08-Jul-15	HK Working		Roof - Scaffolding Erection for Roof				
S9B-T2-B3-3180	Roof - Formwork	9	09-Jul-15	18-Jul-15	HK Working		Roof - Formwork				
Bay 4						73	21-Apr-15	18-Jul-15			
S9B-T2-B4-3040	Wall (North) - Rebar Fixing	3	21-Apr-15	23-Apr-15	HK Working		Wall (North) - Rebar Fixing				
S9B-T2-B4-3050	Wall (Middle) - Formwork & Concrete	3	23-Apr-15	25-Apr-15	HK Working		Wall (Middle) - Formwork & Concrete				
S9B-T2-B4-3060	Wall (South) - Formwork & Concrete	3	11-May-15	13-May-15	HK Working		Wall (South) - Formwork & Concrete				
S9B-T2-B4-3070	Wall (North) - Formwork & Concrete	3	11-May-15	13-May-15	HK Working		Wall (North) - Formwork & Concrete				
S9B-T2-B4-3080	Wall (Middle) - Curing & Formwork Removal	3	26-Apr-15	28-Apr-15	Calendar Day		Wall (Middle) - Curing & Formwork Removal				
S9B-T2-B4-3090	Wall (South) - Curing & Formwork Removal	3	14-May-15	16-May-15	Calendar Day		Wall (South) - Curing & Formwork Removal				
S9B-T2-B4-3100	Wall (North) - Curing & Formwork Removal	3	14-May-15	16-May-15	Calendar Day		Wall (North) - Curing & Formwork Removal				
S9B-T2-B4-3110	OHVD Base Slab - Scaffolding Erection	9	26-May-15	04-Jun-15	HK Working		OHVD Base Slab - Scaffolding Erection				
S9B-T2-B4-3120	OHVD Base Slab - Waterproofing to Upper Side Wall	4	05-Jun-15	09-Jun-15	HK Working		OHVD Base Slab - Waterproofing to Upper Side Wall				
S9B-T2-B4-3130	OHVD Base Slab - Formwork	10	10-Jun-15	22-Jun-15	HK Working		OHVD Base Slab - Formwork				
S9B-T2-B4-3140	OHVD Base Slab - Rebar Fixing	4	23-Jun-15	26-Jun-15	HK Working		OHVD Base Slab - Rebar Fixing				
S9B-T2-B4-3150	OHVD Base Slab - Concrete, Curing & Formwork Dismantling	14	27-Jun-15	10-Jul-15	Calendar Day		OHVD Base Slab - Concrete, Curing & Formwork Dismantling				
S9B-T2-B4-3160	OHVD Hanger Wall - Formwork, Rebar & Concrete	3	30-Jun-15	03-Jul-15	HK Working		OHVD Hanger Wall - Formwork, Rebar & Concrete				
S9B-T2-B4-3170	Roof - Scaffolding Erection for Roof	7	11-Jul-15	18-Jul-15	HK Working		Roof - Scaffolding Erection for Roof				
Bay 5						76	21-Apr-15	22-Jul-15			
S9B-T2-B5-3010	Wall (Middle) - Rebar Fixing	4	21-Apr-15	24-Apr-15	HK Working		Wall (Middle) - Rebar Fixing				
S9B-T2-B5-3030	Wall (South) - Rebar Fixing	3	21-Apr-15	23-Apr-15	HK Working		Wall (South) - Rebar Fixing				
S9B-T2-B5-3040	Wall (North) - Rebar Fixing	3	21-Apr-15	23-Apr-15	HK Working		Wall (North) - Rebar Fixing				
S9B-T2-B5-3050	Wall (Middle) - Formwork & Concrete	3	29-Apr-15	02-May-15	HK Working		Wall (Middle) - Formwork & Concrete				
S9B-T2-B5-3060	Wall (South) - Formwork & Concrete	3	18-May-15	20-May-15	HK Working		Wall (South) - Formwork & Concrete				
S9B-T2-B5-3070	Wall (North) - Formwork & Concrete	3	18-May-15	20-May-15	HK Working		Wall (North) - Formwork & Concrete				
S9B-T2-B5-3080	Wall (Middle) - Curing & Formwork Removal	3	03-May-15	05-May-15	Calendar Day		Wall (Middle) - Curing & Formwork Removal				
S9B-T2-B5-3090	Wall (South) - Curing & Formwork Removal	3	21-May-15	23-May-15	Calendar Day		Wall (South) - Curing & Formwork Removal				
S9B-T2-B5-3100	Wall (North) - Curing & Formwork Removal	3	21-May-15	23-May-15	Calendar Day		Wall (North) - Curing & Formwork Removal				
S9B-T2-B5-3110	OHVD Base Slab - Scaffolding Erection	9	05-Jun-15	15-Jun-15	HK Working		OHVD Base Slab - Scaffolding Erection				
S9B-T2-B5-3120	OHVD Base Slab - Waterproofing to Upper Side Wall	4	16-Jun-15	19-Jun-15	HK Working		OHVD Base Slab - Waterproofing to Upper Side Wall				
S9B-T2-B5-3130	OHVD Base Slab - Formwork	10	22-Jun-15	03-Jul-15	HK Working		OHVD Base Slab - Formwork				
S9B-T2-B5-3140	OHVD Base Slab - Rebar Fixing	4	04-Jul-15	08-Jul-15	HK Working		OHVD Base Slab - Rebar Fixing				
S9B-T2-B5-3150	OHVD Base Slab - Concrete, Curing & Formwork Dismantling	14	09-Jul-15	22-Jul-15	Calendar Day		OHVD Base Slab - Concrete, Curing & Formwork Dismantling				
S9B-T2-B5-3160	OHVD Hanger Wall - Formwork, Rebar & Concrete	3	13-Jul-15	15-Jul-15	HK Working		OHVD Hanger Wall - Formwork, Rebar & Concrete				
Bay 6						58	15-May-15	24-Jul-15			
S9B-T2-B6-1010	Base Slab - Waterproofing	4	15-May-15	19-May-15	HK Working		Base Slab - Waterproofing				
S9B-T2-B6-1020	Base Slab - Formwork & Rebar Fixing	14	20-May-15	05-Jun-15	HK Working		Base Slab - Formwork & Rebar Fixing				
S9B-T2-B6-1030	Base Slab - Concrete & Curing	5	06-Jun-15	10-Jun-15	Calendar Day		Base Slab - Concrete & Curing				
S9B-T2-B6-3000	Wall (South) - Waterproofing	4	11-Jun-15	15-Jun-15	HK Working		Wall (South) - Waterproofing				
S9B-T2-B6-3010	Wall (Middle) - Rebar Fixing	4	11-Jun-15	15-Jun-15	HK Working		Wall (Middle) - Rebar Fixing				
S9B-T2-B6-3020	Wall (North) - Waterproofing	4	11-Jun-15	15-Jun-15	HK Working		Wall (North) - Waterproofing				

Activity ID	Activity Name	OD	Start	Finish	Calendar	2015					
						Apr	May	Jun	Jul	Aug	
						64	65	66	67	68	
S9B-T2-B6-3030	Wall (South) - Rebar Fixing	3	16-Jun-15	18-Jun-15	HK Working			■	Wall (South) - Rebar Fixing		
S9B-T2-B6-3040	Wall (North) - Rebar Fixing	3	16-Jun-15	18-Jun-15	HK Working			■	Wall (North) - Rebar Fixing		
S9B-T2-B6-3050	Wall (Middle) - Formwork & Concrete	3	16-Jun-15	18-Jun-15	HK Working			■	Wall (Middle) - Formwork & Concrete		
S9B-T2-B6-3060	Wall (South) - Formwork & Concrete	3	19-Jun-15	23-Jun-15	HK Working			■	Wall (South) - Formwork & Concrete		
S9B-T2-B6-3070	Wall (North) - Formwork & Concrete	3	19-Jun-15	23-Jun-15	HK Working			■	Wall (North) - Formwork & Concrete		
S9B-T2-B6-3080	Wall (Middle) - Curing & Formwork Removal	3	19-Jun-15	21-Jun-15	Calendar Day			■	Wall (Middle) - Curing & Formwork Removal		
S9B-T2-B6-3090	Wall (South) - Curing & Formwork Removal	3	24-Jun-15	26-Jun-15	Calendar Day			■	Wall (South) - Curing & Formwork Removal		
S9B-T2-B6-3100	Wall (North) - Curing & Formwork Removal	3	24-Jun-15	26-Jun-15	Calendar Day			■	Wall (North) - Curing & Formwork Removal		
S9B-T2-B6-3110	OHVD Base Slab - Scaffolding Erection	9	27-Jun-15	08-Jul-15	HK Working				■	OHVD Base Slab - Scaffolding Erection	
S9B-T2-B6-3120	OHVD Base Slab - Waterproofing to Upper Side Wall	4	09-Jul-15	13-Jul-15	HK Working				■	OHVD Base Slab - Waterproofing to Upper Side	
S9B-T2-B6-3130	OHVD Base Slab - Formwork	10	14-Jul-15	24-Jul-15	HK Working				■	OHVD Base Slab - Formwork	
Tunnel Portion 3 & Tunnel Portion 4 (CH3630-CH3790)		269	11-Mar-15 A	19-Jan-16	HK Working						
Foundation		7	18-Apr-15 A	25-Apr-15	HK Working						
Stage 4 - Southern Wall after HHR Flyover Diversion (Stage 2) (P132-P143)		7	18-Apr-15 A	25-Apr-15	HK Working						
S9B-T34-1700	Tunnel Portion 3 & 4 Pumping test	7	18-Apr-15 A	25-Apr-15	HK Working		■				
CWB Structural Works		250	11-Mar-15 A	19-Jan-16	HK Working						
S9B-T34-2000B	Tunnel Portion 3 & 4 Excavation (200,000m3 soil @800m3/d) & ELS	250	11-Mar-15 A	19-Jan-16	HK Working						
Section 10 Works - CWB Tunnel Structure (CH3246 - CH3400)		90	07-May-15	22-Aug-15	HK Working						
Tunnel Portion 6 (CH3246-CH3280)		90	07-May-15	22-Aug-15	HK Working						
S10-T6-1020	Tunnel Portion 6 Bored Pile - 13nr. (2 sets @ 14d/pile)	90	07-May-15	22-Aug-15	HK Working						
Section 11 of the Works - Remainder of Works		194	13-Feb-15 A	30-Sep-15	Calendar Day						
Marine Works at WCR3		194	13-Feb-15 A	30-Sep-15	Calendar Day						
S11-R3-1210B	Air lifting for removal of sunken objects (VO203)	138	13-Feb-15 A	30-Jun-15	Calendar Day						
S11-R3-1210C	Removal of sunken objects	92	01-Jul-15	30-Sep-15	Calendar Day						
Soft Landscaping & Establishment Works		2375	24-Feb-10 A	29-Aug-16	Calendar Day						
Section 8D of the Works - Establishment Works in Area 8		365	21-Apr-15	19-Apr-16	Calendar Day						
S8D-0010	Carry out establishment work on new ferry pier	365	21-Apr-15	19-Apr-16	Calendar Day						
Section 12 of the Works - Protection and Preservation of Existing Trees		2375	24-Feb-10 A	29-Aug-16	Calendar Day						
S12-0010	Protection and preservation of existing trees	2375	24-Feb-10 A	29-Aug-16	Calendar Day						
SUMMARY PROGRAMME		947	07-May-13 A	08-May-16	Calendar Day						
CWB Tunnel Construction & Remaining Works (Section 9A, 9B, 10 & 11)		480	30-Aug-14 A	08-May-16	Calendar Day						
CWB Tunnel Works in WCR2		261	19-Jan-15 A	26-Sep-15	Calendar Day						
SUM-CWB-23000	CWB Tunnel Portion 2 Construction	261	19-Jan-15 A	26-Sep-15	Calendar Day						
CWB Tunnel Works in WCR3		358	30-Aug-14 A	08-May-16	Calendar Day						
SUM-CWB-30000	Reclamation at WCR3 & Ferry Pier Demolition (Except Water Channel Maintained for HK/200	209	30-Aug-14 A	08-May-16	Calendar Day						
SUM-CWB-35000B	Foundation for Tunnel Portion 6 - Bored Pile	108	07-May-15	22-Aug-15	Calendar Day						
CWB Tunnel Works in WCR4/TWCR4		249	11-Mar-15 A	19-Jan-16	Calendar Day						
SUM-CWB-42000	Pump Test & Excavation for Tunnel Portion 3&4	249	11-Mar-15 A	19-Jan-16	Calendar Day						
Reprovisioning of Existing Facilities (Section 3, 4A, 4B, 4C, 5, 6, 7, 8A & 8B)		754	07-May-13 A	04-May-15	Calendar Day						
Reprovisioning of Box Culvert N (Section 7)		249	08-Oct-14 A	04-May-15	Calendar Day						
SUM-FAC-52000	VO116 - New Transformer Building to Ferry Pier	249	08-Oct-14 A	04-May-15	Calendar Day						
Reprovisioning of Wan Chai Ferry Pier & Covered Walkway (Section 8A & 8B)		150	07-May-13 A	30-Apr-15	Calendar Day						
SUM-FAC-65000	ABWF Works on Observation Deck under Section 8B	150	07-May-13 A	30-Apr-15	Calendar Day						

SR8_DWP_06(A)-MU24		SR8 - Layout for 3MRP_2105_03			Appendix C.5											
Activity ID	Activity Name	Original Duration	Start	Finish	2015											
					Mar			Apr			May			Jun		
DWP-06 (A) - Update Progress As of 20 Mar 15																
Works in TS3																
TS3 East & West Reclamation Works																
TS3W - Reclamation Works (new scheme)																
TS3W.MW.2110	TS3W - General Fill Area 2 (3 Barges)	40	20-Dec-14 A	25-Mar-15	TS3W - General Fill Area 2 (3 Barges)											
TS3W.MW.2140	TS3W - Handover to D-wall (Phase 1)	0		20-Mar-15	TS3W - Handover to D-wall (Phase 1)											
TS3W.MW.2120	TS3W - General Fill Area 3 (1 Barges)	22	08-Apr-15	29-Apr-15	TS3W - General Fill Area 3 (1 Barges)											
TS3W.MW.2190	TS3W - Completion of Reclamation Works	0		29-Apr-15	TS3W - Completion of Reclamation Works											
TS3W - North																
TS3W.MW.2040	TS3W North - Rockfill	21	21-Jan-15 A	21-Mar-15	TS3W North - Rockfill											
TS3W.MW.2040A	TS3W North - Levelling	4	22-Mar-15	25-Mar-15	TS3W North - Levelling											
TS3W.MW.2060	TS3W North - Phase 2 Seawall Block Installation	13	26-Mar-15	07-Apr-15	TS3W North - Phase 2 Seawall Block Installation											
Works in TS3-East																
Diaphragm Wall																
TS3-East Diaphragm Construction																
TS3E_3120	Diaphragm wall construction Phase 2 (34/50 panels @ proposed bulkhead)	80	21-Feb-15 A	28-Apr-15	Diaphragm wall construction Phase 2 (34/50 panels @ proposed bulkhead)											
Works in SR8 (Open Cut Method)																
SR8 - Cofferdam & Cut & Cover Tunnel Works																
SR8 East Bound - (Seaside to Victoria Road / IEC Central Divider)																
Method Statement																
ELS																
SR8_2260	ELS Method statement - submission	24	29-May-15	26-Jun-15												
TTA Stage 1 - East Bound																
Stage 2 - East Bound (Ref. DRG. No.CDD/SR8/083)																
SR8.EB.1530	Construct IEC East Bound Up Ramp	60	11-Feb-15 A	15-Apr-15	Construct IEC East Bound Up Ramp											
SR8.EB.1385	Install Dewatering Wells and Observation Wells & Pump Test	14	11-Mar-15 A	20-Mar-15 A	Install Dewatering Wells and Observation Wells & Pump Test											
SR8.EB.1390	Construct Traffic Deck	35	18-Mar-15 A	02-Apr-15	Construct Traffic Deck											
SR8.EB.1380	Demolish part of the Wing Wall of Abutment M	14	20-Mar-15	09-Apr-15	Demolish part of the Wing Wall of Abutment M											
TTA Stage 2 - East Bound																
Stage 3 - East Bound (Ref. DRG. No.CDD/SR8/084)																
SR8.EB.1410	Implement TTA Stage 2 - Traffic Diversion at East Bound (DRG REF.4843/011/030B and 4843/011/040B)	0	19-Apr-15		Implement TTA Stage 2 - Traffic Diversion at East Bound (DRG REF.4843/011/030B and 4843/011/040B)											
SR8.EB.1420	Demolish Part of EB Existing Abutment M and Part of the Central Divider	12	20-Apr-15	04-May-15	Demolish Part of EB Existing Abutment M and Part of the Central Divider											
SR8.EB.1430	Carry out Pre-boring for Sheet Pile	24	20-Apr-15	18-May-15	Carry out Pre-boring for Sheet Pile											
SR8.EB.1440	Carry out Stage 3 - Sheet Pile Work	21	13-May-15	06-Jun-15	Carry out Stage 3 - Sheet Pile Work											
		<div><div></div> Actual Work</div> <div><div></div> Remaining Work</div> <div><div></div> Critical Remaining Work</div> <div><div></div> Milestone</div>		Page 1 of 5 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Programme					Date 20-Mar-15		Revision Updated to 20th March 2015		Checked DML/WC		Approved	

Activity ID		Activity Name		Original Duration	Start	Finish	2015																																							
							Mar							Apr							May							Jun																		
SR8.EB.1450							Carry out Stage 3 - Pipe Piling Work							60	05-Jun-15		15-Aug-15																													
Stage 4 - East Bound (Ref. DRG. No.CDD/SR8/084)																																														
SR8.EB.1470							Commence Stage 4 (After Completion of reclamation works)							0	08-Jun-15																															
SR8.EB.1480							Carry out Stage 4 Sheet Piling Works							24	08-Jun-15		07-Jul-15																													
SR8 West Bound - Ch. 459.000 to 385.000 (Victoria Road / IEC Central Divider)																																														
TTA Stage 2 - West Bound																																														
Stage 3 - West Bound (Ref. DRG. No.CDD/SR8/087)																																														
SR8.WB.3030							Carry out Stage 3 Sheet Pile works							27	17-Feb-15 A		20-Mar-15 A																													
SR8.WB.3040							Carry out Stage 3 Pipe Piling Works							45	20-Mar-15 A		16-May-15																													
SR8.WB.3050							Carry out Stage 3 TAM Grout							17	18-May-15		06-Jun-15																													
SR8.WB.3060							Install Dewatering Wells & Carry out Pump Test							20	08-Jun-15		02-Jul-15																													
SR8 Ch.385.000 to Ch.317.500 - (Inside Victoria Park to Tunnel Portal)																																														
SR8 Tunnel - ELS / CCT / BF Works (7 Bays Ch. 385.000 to Ch.317.500)																																														
ELS																																														
SR8.VP.5070A							ELS Layer 3 - Soft Excavation + Strut Installation							8	11-Feb-15 A		18-Apr-15																													
SR8.VP.5080							Soft Excavation down to Formation Level							16	20-Apr-15		08-May-15																													
Portal Structure																																														
Blinding + Waterproofing																																														
SR8.VP.5030							Blinding for Bay 1 to Bay 7							7	08-May-15		16-May-15																													
SR8.VP.5090							Waterproofing for Bay 1 to Bay 7							7	18-May-15		26-May-15																													
Base Slab + Drainage																																														
SR8.VP.5100							Base Slab - Bay 1							8	27-May-15		04-Jun-15																													
SR8.VP.5110							Base Slab - Bay 2							8	05-Jun-15		13-Jun-15																													
SR8.VP.5120							Base Slab - Bay 3							8	15-Jun-15		24-Jun-15																													
Pump Sump E																																														
SR8.VP.5360							Base Slab							8	27-May-15		04-Jun-15																													
SR8.VP.5370							Wall Up to Portal Base Slab Bottom							10	05-Jun-15		16-Jun-15																													
SR8.VP.5380							Fill Up Void Up to Portal Base Slab Bottom							7	17-Jun-15		25-Jun-15																													
SR8 Ch 317.500 to Ch 210.000 - U-Structure & Slab (Victoria Park)																																														
Excavation and Lateral Support																																														
SR8_2300							Form Temporary Access to Bowling Green at Bay 3(CH230 to CH240)							7	20-Mar-15 A		11-Apr-15																													
SR8_2310							ELS - Excavation to Formation Level + Lateral Support for UBA2 to UBA5							21	13-Apr-15		07-May-15																													
RC CCT & Backfill Ch317.5000 to Ch240.000																																														
Structure																																														
Blinding + Waterproofing																																														

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Page 2 of 5

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Programme

Date

Revision

Checked

Approved

20-Mar-15

Updated to 20th March 2015

DML/WC

Activity ID	Activity Name	Original Duration	Start	Finish	2015											
					Mar			Apr			May			Jun		
	SR8_1830	Blinding & Waterproofing Bay UBA2 to UBA5	4	08-May-15	12-May-15											
	SR8_1840	Remove Bulk Head at CH317.5	7	09-May-15	16-May-15											
	SR8_1860	Blinding & Waterproofing Bay UBA8	4	18-May-15	21-May-15											
	Base Slab															
	SR8_1801	Remove SL3 - (UBA6 - UBA7 & UBA1)	14	20-Mar-15	09-Apr-15											
	SR8_1810	SR8 U-structure Base slab (UBA2 - UBA5)	48	13-May-15	10-Jul-15											
	SR8_1812	SR8 U-structure Base slab (UBA8)	24	22-May-15	19-Jun-15											
	Wall															
	SR8_1850B	SR8 U-structure Wall (UBA6-UBA7) - Stage 2	14	23-Feb-15 A	25-Apr-15											
	SR8_1850A	Remove SL2, 1 (UBA6-UBA7)	14	20-Mar-15	09-Apr-15											
Tsing Fung St - RW & Subway Extension & Toe Wall at Hing Fat St																
Ret. Wall & TF Subway Extension (Portion V)																
Retaining Wall RW8C at Tsing Fung Street (Portion V)																
	VP_1370	TFS New Ret. Wall - backfilling & compactionworks	24	01-Dec-14 A	02-Apr-15											
	VP_1770	Install Steel Railing on Top of RW8C	14	08-Apr-15	23-Apr-15											
	VP_1390	Demolish Top Portion of Existing Wall Head and Kerb	18	23-Apr-15	15-May-15											
	VP_1400	Road Formation - Subbase + Kerb + U-shape Channel	48	15-May-15	14-Jul-15											
Retaining Wall + Toe Wall at Hing Fat Street																
Subway Extension at Tsing Fung Street (Portion VIII)																
West Side																
	VP_1330	Divert Footpath for Closing West Part of Subway	2	24-Apr-15	25-Apr-15											
	VP_1365	Excavation and Demolition (West Part) of Subway	14	27-Apr-15	13-May-15											
	VP_1375.10	TFS Subway extension - Blinding and Waterproofing	8	14-May-15	22-May-15											
	VP_1375.20	TFS Subway extension - Base slab + Drainage	21	23-May-15	17-Jun-15											
	VP_1375.30	TFS Subway extension - Walls	18	18-Jun-15	10-Jul-15											
Tree Transplanting at Portion VIII (Tree Zone 20) (6 trees)																
	VP_1700	Preparation and Site Hoarding	36	19-Sep-14 A	23-Apr-15											
RC Works - Toe Wall (RW8E)																
	VP_6152	Construct and divert Temporary Footpath	36	24-Apr-15	06-Jun-15											
	VP_6160	Sheet Piling and Excavation to Formation level	45	08-Jun-15	31-Jul-15											
Works in Victoria Park																
Re-Provisioning Works																
Pavilion																
Temp. Works Design																
	VP_0230	(01) Temp. Work Design - review and approval by AECOM	24	27-Feb-15 A	31-Mar-15											

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Page 3 of 5

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
20-Mar-15	Updated to 20th March 2015	DML/WC	

Activity ID		Activity Name		Original Duration	Start	Finish	2015														
							Mar			Apr			May			Jun					
Materials Submission																					
VP_6650		Materials - ER review and approval		24	23-Feb-15 A	31-Mar-15	Materials - ER review and approval														
VP_6660		Issue P.O. / Manufacturing / Fabrication		48	01-Apr-15	02-Jun-15	Issue P.O. / Manufacturing / Fabrication														
Shop Drawings																					
VP_0195		Shopdrawing submission		7	12-Mar-15 A	11-Apr-15	Shopdrawing submission														
VP_0215		Shopdrawing - ER review and approval		24	13-Apr-15	11-May-15	Shopdrawing - ER review and approval														
Method Statement																					
VP_6680		(01) Method statement - submission		7	01-Apr-15	13-Apr-15	(01) Method statement - submission														
VP_6690		(01)Method statement - review and approval by AECOM		24	14-Apr-15	12-May-15	(01)Method statement - review and approval by AECOM														
Construction Works - BG Pavillion																					
VP_1310		PV - Site Possession, Portion VI/VII		0	20-Mar-15		PV - Site Possession, Portion VI/VII														
VP_1340		Demolish existing BGO		24	01-Apr-15	04-May-15	Demolish existing BGO														
VP_1300		PV - Initial works (Site Clearance, underground utilities etc.)		24	05-May-15	02-Jun-15	PV - Initial works (Site Clearance, underground utilities etc.)														
VP_1360		PV - foundation works		21	19-May-15	12-Jun-15	PV - foundation works														
VP_1380		PV- structural works, G/F to Roof		24	10-Jun-15	09-Jul-15	PV- structural works, G/F to Roof														
Bowling Green																					
Design Submissions for Bowling Green Lighting																					
VP_0330		Engineer's Review and Approval		24	23-Sep-14 A	27-Mar-15	Engineer's Review and Approval														
Method Statement																					
VP_0260		(01)Method statement - review and approval by AECOM		24	20-Nov-14 A	31-Mar-15	(01)Method statement - review and approval by AECOM														
Procurement																					
VP_1010.174		Materials - ER review and approval		24	14-Feb-15 A	29-Apr-15	Materials - ER review and approval														
VP_1010.184		Issue PO / Manufacturing		42	30-Apr-15	19-Jun-15	Issue PO / Manufacturing														
VP_6670		Materials Delivery - Green Turf		24	03-Jun-15	02-Jul-15	Materials Delivery - Green Turf														
Portion VII Tree Transplanting, DBH <300mm																					
VP_1330.04		<300mm dia trees (3months) - Stage 4 root pruning & removal/Transplanting		12	05-Nov-14 A	02-Apr-15	<300mm dia trees (3months) - Stage 4 root pruning & removal/Transplanting														
Construction Works																					
VP_1320		BG - Site Possession, Portion VI, VII		0	20-Mar-15		BG - Site Possession, Portion VI, VII														
VP_1170		Demolish existing CP / BGO / Site Clearance		24	01-Apr-15	04-May-15	Demolish existing CP / BGO / Site Clearance														
VP_1180		Site Survey / Setting up		12	05-May-15	18-May-15	Site Survey / Setting up														
VP_1710		BG - Install U/G Sewerage System		24	12-May-15	09-Jun-15	BG - Install U/G Sewerage System														
VP_1720		BG - Install Drainage System		24	27-May-15	24-Jun-15	BG - Install Drainage System														
VP_1730		BG - Install Irrigation System		24	10-Jun-15	09-Jul-15	BG - Install Irrigation System														
Mooring Components Upkeep (CBTS and ATS)																					
MAR_2000		Mooring Upkeep at Portion XIX(19) & XX(20) - ATS (if instructed by Engineer)		1399	21-Mar-13 A	17-Jan-17	Mooring Upkeep at Portion XIX(19) & XX(20) - ATS (if instructed by Engineer)														
				Page 4 of 5			Date			Revision			Checked			Approved					
				Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Programme			20-Mar-15			Updated to 20th March 2015			DML/WC								

Activity ID		Activity Name	Original Duration	Start	Finish	2015																											
						Mar							Apr							May							Jun						
MAR_1000		Mooring Upkeep at Portion III (3) - CBTS	574	15-May-14 A	09-Dec-15																												
MAR_3020		Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979	15-May-14 A	17-Jan-17																												
Works for Public Works Regional Laboratory (North Lantau)																																	
Maintenance and Upkeep of New PWRL (Portion XVII)																																	
PWRL_1050		Maintenance/ Upkeep of New PWRL	1301	19-Jul-13 A	21-Nov-17																												

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Page 5 of 5

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Progamme

Date	Revision	Checked	Approved
20-Mar-15	Updated to 20th March 2015	DML/WC	
