



DRAINAGE SERVICES DEPARTMENT
CONTRACT NO. DC/2011/06
REPROVISIONING OF BOUNDARY PATROL ROAD AND
ASSOCIATED SECURITY FACILITIES BETWEEN
PING YUEN RIVER AND PAK FU SHAN AND
DRAINAGE WORKS IN NORTH DISTRICT
MONTHLY EM&A REPORT FOR
ADVANCED WORKS UNDER EP-430/2011
(NOVEMBER 2012)

PREPARED FOR
SANG HING CIVIL CONSTRUCTORS CO., LTD.

Quality Index

Date	Reference No.	Prepared By	Approval By
12 December 2012	TCS00599/12/600/R0062v1	 F. N. Wong Senior Environmental Consultant	 T. W. Tam Environmental Team Leader

Version	Date	Description
0	7 December 2012	First submission.
1	12 December 2012	Amended against IEC's comments.

This report has been prepared by Action-United Environmental Services & Consulting with all reasonable skill, care and diligence within the terms of the Agreement with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies upon the report at their own risk.

Ref.: DSDBPRNDEM00_0_0087L.12

12 December 2012

By Post and Fax (2959 6079)

Action-United Environmental Services & Consulting
Unit A, 20/F,
Gold King Industrial Building,
New Territories, Hong Kong

Attention: Mr. TW Tam

Dear Sir,

**Re: Contract No. DC/2011/06
Reprovisioning of Boundary Patrol Road and Associated Security Facilities
between Ping Yuen River and Pak Fu Shan and Drainage Works in North
District
EM&A report for Advanced Works under EP-430/2011 (November 2012)**

Reference is made to the Environmental Team's submission of the captioned report (Version 1) dated 7 December 2012 received through E-mail on 7 December 2012 for our review and comment.

Please be informed that we have no further comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 5.4 in the captioned Environmental Permit.

Thank you for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



Roger Leung
Independent Environmental Checker

c.c. DSD Mr. W.H. Poon by fax: 2827 8700
 SHCCCL Mr. Raymond W.M. Yau by fax: 2403 1162

Q:\Projects\DSDBPRNDEM00\02 Project Management\02 Corr\DSDBPRNDEM00_0_0087L.12.doc

EXECUTIVE SUMMARY

BREACHES OF ACTION AND LIMIT LEVELS

- ES01. No environmental monitoring is required for construction of the Works, no breaches of Action and Limit levels are therefore applicable for the Works.

REPORTING CHANGES

- ES02. No reporting changes were made during the Reporting Period.

COMPLAINTS LOG

- ES03. No environmental complaint was registered during the Reporting Period. The complaint log is presented as follows:

Reporting Month	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
August to October 2012	0	0	Not Applicable
November 2012	0	0	Not Applicable

NOTIFICATIONS OF ANY SUMMONS AND SUCCESSFUL PROSECUTIONS

- ES04. No notifications of any summons and successful prosecutions were registered during the Reporting Period.
- ES05. No non-compliance with the regulatory requirements was identified in the site inspection during the Reporting Period, including the regular joint site inspection by the ER, IEC, ET and Contractor. Defects of minor environmental significance were sometimes identified and normally rectified in-situ or within the specified time prior to the next site inspection.

FORECAST OF IMPACT PREDICTIONS

- ES06. Construction dust, noise and water quality continue to be the key environmental issues for the coming construction period.

RECOMMENDATIONS

- ES07. The Contractor is reminded to fully comply with all the relevant regulatory environmental requirements, including environmental mitigation measures stipulated in all the environmental ordinances, EM&A Manual, EMP and the associated WMP, effluent discharge license and the chemical waste producer registration, etc.
- ES08. Particular attention is drawn to full implementation of air quality mitigation measures, in particular construction dust suppression measures during dusty construction activities under dry and windy conditions.
- ES09. In addition, full implementation of the required water quality mitigation measures is reminded to eliminate adverse water quality impacts generated from surfaces of haul roads, stock pile of excavated materials, etc. during wet season.
- ES10. Moreover, construction noise mitigation measures shall also be implemented during noisy construction works.

TABLE OF CONTENTS

1	BACKGROUND INFORMATION	- 4 -
2	SUMMARY OF EM&A REQUIREMENTS FOR THE WORKS.....	- 5 -
3	DATA MANAGEMENT AND DATA QA/QC CONTROL.....	- 6 -
4	ENVIRONMENTAL LICENSES AND PERMITS	- 7 -
5	WASTE MANAGEMENT.....	- 10 -
6	SITE INSPECTION AND ENVIRONMENTAL AUDIT	- 10 -
7	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	- 11 -
8	IMPACT FORECAST	- 11 -
9	CONCLUSIONS AND RECOMMENDATIONS.....	- 12 -

LIST OF TABLES

TABLE 4-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMIT
TABLE 4-2	MAJOR CONSTRUCTION ACTIVITIES OF THE WORKS DURING THE REPORTING PERIOD
TABLE 4-3	MAJOR CONSTRUCTION ACTIVITIES OF THE WORKS FOR THE FORTHCOMING TWO MONTHS
TABLE 6-1	OBSERVATIONS OF SITE INSPECTION DURING THE REPORTING PERIOD
TABLE 7-1	SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 7-2	SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 7-3	SUMMARY OF ENVIRONMENTAL PROSECUTION

LIST OF ANNEXES

ANNEX A	LOCATION PLAN FOR THE WORKS
ANNEX B	ENVIRONMENTAL MANAGEMENT ORGANIZATION AND COMMUNICATION LINES
ANNEX C	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES
ANNEX D	THREE-MONTH ROLLING PROGRAM
ANNEX E	MONTHLY SUMMARY WASTE FLOW TABLE/SUMMARY TABLE FOR WORK PROCESSES OR ACTIVITIES REQUIRING TIMBER FOR TEMPORARY WORKS

1 BACKGROUND INFORMATION

DSD CONTRACT NO. DC/2011/06

- 1.01 Sang Hing Civil Contractors Company Limited (hereinafter “SHCCCL” or “the Contractor”) has been awarded by Drainage Services Department of the HKSAR Government (hereinafter “DSD” or “the Engineer”) since 31 March 2012 DSD Contract No. DC/2011/06 – Reprovisioning of Boundary Patrol Road and Associated Security Facilities between Ping Yuen River and Pak Fu Shan and Drainage Works in North District (hereafter “the Contract”).
- 1.02 The Contract comprises:
- A. Reprovisioning of Boundary Patrol Road and Associated Security Facilities between Ping Yuen River and Pak Fu Shan**, which is one of the two parts of Regulation of Shenzhen River Stage 4, i.e. the Advanced Works within the HKSAR to be implemented under Environmental Permit No. EP-430/2011 (hereinafter “EP-430/2011”) (hereinafter “the Advanced Works under EP-430/2011” or “the Works”). The Works include:
- 1) Reprovisioning of approximately 4.3 kilometres (km) long and 3.5 metres (m) wide boundary patrol road between Ping Yuen River and Pak Fu Shan;
 - 2) Reprovisioning of approximately 4.3 km long primary boundary fence with associated lighting and Fence Protection System between Ping Yuen River and Pak Fu Shan;
 - 3) Reprovisioning of the Hong Kong Police Force Lo Fong Bridge Post; and
 - 4) Construction of about 3.3 km long secondary boundary fence.
- B. Drainage Works in North District to be implemented under Environmental Permit No. EP-277/2007/A**, which has been commenced in May 2012 and is scheduled to be completed by May 2013, including
- 1) Construction of about 400m of drainage channel at Man Uk Pin under Environmental Permit No. EP-277/2007/A (hereinafter “EP-277/2007/A”);
 - 2) The associated ancillary works including drainage and landscaping works.
- C. Drainage Works in North District**, which is a non-designated project of drainage works at Ma Wat Wai in North District for construction of about 110 m of drainage channel at Ma Wat Wai.
- 1.03 Drawing of the area within the Works showing is shown in **Annex A**, whereas project organization, environmental management structure and communication lines, including contacts of key personnel under the Contract as well as the 3-monthly rolling program covering the second month of the construction of the Works are shown in **Annex B**.
- 1.04 Construction of the Advanced Works under EP-430/2011 has been commenced on 21 August 2012 after site clearance and the associated preparation works as well as completion of submission required under EP-430/2011. The Works is to be completed in August 2014 within 29 months.

CONCURRENT PROJECTS IN THE VICINITY OF THE WORKS

- 1.05 The following projects are anticipated to be carried out concurrently in the vicinity of the Works:
- 1) The River Modification Works within HKSAR, which is part of the Regulation of Shenzhen River Stage 4 and to be implemented under EP-430/2011, is scheduled for commencement in mid-2013.
 - 2) The development of the proposed Liantang/Heung Yuen Wai Boundary Control Point (hereinafter “the LT/HYW BCP”) and the associated works. It is anticipated that the construction of the LT/HYW BCP and connecting roads will commence at the end of 2013 and be completed in end 2018. The planned construction period for the resite of Chuk Yuen Village is from late 2010 to early 2012 for population intake by early 2013.
 - 3) Construction of a Secondary Boundary Fence and New Sections of Primary Boundary fence and Patrol Road. Based on the advice from ArchSD, the latest tentative construction programme shall be from end 2011 to early 2013 (section from Ng Tung River to Ping Yuen River) and from end 2011 to end 2013 (section from Pak Fu Shan to Lin Ma Hang Road).
 - 4) Drainage Improvement in Northern New Territories, Package C (Remaining Works). The construction work is scheduled to commence in late 2012 and completed by 2016.

CUMULATIVE ENVIRONMENTAL IMPACTS

- 1.06 As concluded in the EIA report for Regulation of Shenzhen River Stage 4, adverse environmental impacts generated from the River Modification Works within HKSAR are predicted to be minimal provided the required environmental mitigation measures are fully implemented.
- 1.07 There is a potential of cumulative environmental impacts during construction phase, including construction dust, noise, water quality, waste, ecology and landscape and visual, to be generated from the concurrent works LT/HYW BCP and the associated works as well as construction of a secondary boundary fence and new sections of primary boundary fence and patrol road.
- 1.08 However, as the schedules and programs of those concurrent projects are subject to private initiatives and market-driven factors, it is not possible to assess the cumulative impact at this stage.
- 1.09 On the other hand, the Drainage Improvement in Northern New Territories, Package C (Remaining Works) project is subject to another future detailed EIA Study and detailed construction program is not available to date. The cumulative impact cannot be assessed at this stage. However, since the drainage improvement works is located at about 500 m from the Site and given its nature and scale of works, adverse cumulative environmental impacts are not anticipated.

2 SUMMARY OF EM&A REQUIREMENTS FOR THE WORKS

CONSTRUCTION ACTIVITIES UNDER THE WORKS

- 2.01 Construction activities under the Works comprise:
- 1) Approximately 4,300 m of 3.5 m wide Boundary Patrol Road on filled embankment along the Shenzhen River from Ping Yuen River estuary and Pak Fu Shan, Ta Kwu Ling;
 - 2) Approximately 4,300 m of Primary Boundary Fence with XPM mesh;
 - 3) Approximately 3,300 m of Secondary Boundary Fence with XPM mesh;
 - 4) Approximately 4,300 m of border security lighting system including the associated electrical and mechanical works;
 - 5) 4 box culverts and 12 drainage pipes under the proposed Boundary Patrol Road, and the associated inlets and outlets;
 - 6) Reconstruction of Lo Fong Bridge Post for Hong Kong Police Force;
 - 7) Peripheral drainage system associated with the above items;
 - 8) Irrigation systems including associated electrical and mechanical works;
 - 9) Landscaping works and environmental mitigation works;
 - 10) Other ancillary works associated with the above items;
- 2.02 The construction areas under the Works are divided into the following three portions:
- 1) Portion A – Area between CH_R 0+000 and 2+050 for reprovisioning of Boundary Patrol Road and the associated security facilities;
 - 2) Portion B – Area between CH_R 2+050 and 2+840 for reprovisioning of Boundary Patrol Road and the associated security facilities;
 - 3) Portion C – Area between CH_R 2+840 and 4+300 approximately for reprovisioning of Boundary Patrol Road and the associated security facilities;

EM&A REQUIREMENTS FOR THE WORKS

CONSTRUCTION PHASE

- 2.03 The EIA report has assessed potential environmental impacts to be generated from the Works. Conclusions and recommendations for EM&A during construction of the Works are presented in the EIA report and the associated Updated EM&A Manual. They are summarized as follows:
- 2.04 No environmental monitoring and audit is required during construction phase of the Works for air quality, construction noise, water quality, ecology, cultural heritage as well as landscape and visual.

OPERATIONAL PHASE

- 2.05 No environmental monitoring and audit is required during operational phase of the Works for air quality, construction noise, water quality, ecology, cultural heritage as well as landscape and visual.

BASELINE MONITORING AND ENVIRONMENTAL QUALITY CRITERIA

- 2.06 As no environmental monitoring is recommended for both construction and operational phases of the Works, baseline monitoring and the associated environmental quality criteria, i.e. Action/ limit Levels, are not required.

EVENT & ACTION PLAN

- 2.07 No Event and Action Plan is recommended for both construction and operational phases. No monitoring and response mechanism for handling exceedances of environmental standards during the construction phase in collaboration with relevant parties of other concurrent projects in the vicinity is therefore applicable during construction of the Works.

ENVIRONMENTAL PROTECTION OF THE WORKS

- 2.08 EIA report has concluded that neither environmental monitoring nor the associated Event and Action Plan is required for the Works, provided environmental mitigation measures stipulated in the EIA report and summarized in the Updated EM&A Manual are fully implemented.
- 2.09 The environmental protection of the Works relies therefore on insurance against non-compliance or defects identified during day-to-day site inspection and environmental audit by related parties of the environmental management under the Works.
- 2.10 It is also crucial to regularly review on compliance with legal and contractual requirements of the Works.
- 2.11 Equally important is proper handling of environmental complaint, enquiries and requests for information as appropriate.

SITE INSPECTION AND ENVIRONMENTAL AUDIT

- 2.12 The ET will undertake site inspection of on-site practices and procedures each month. Joint site inspection and environmental audit is also required to be conducted by related parties of the environmental management to verify the implementation status and evaluate the effectiveness and stability of the environmental mitigation measures, in collaboration with relevant parties of other concurrent projects in the vicinity.
- 2.13 Details of the scope and range of issues to be designed and addressed in the site inspection and environmental audit protocols are presented in *Section 6*.

ENVIRONMENTAL REPORTING OF THE WORKS

- 2.14 In order to ease environmental reporting of the Contract, it has been agreed among the Engineer, IEC, Contractor and ET that the environmental reporting for the Contract is split into three stand-alone reports, namely Environmental Report for Advanced Works under EP-430/2011, EM&A Report for Drainage Works under EP-277/2007/A and EM&A Report for Drainage Works at Ma Wat Wai. They will be prepared and submitted separately.
- 2.15 This is the EM&A report for the Works (herein after “this Report”), covering construction period from 1 to 31 October 2012 (hereinafter “the Reporting Period”).

3 DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.01 The impact monitoring data is handled by the ET’s systematic data recording and management, which complies with an in-house certified (ISO 9001:2000) Quality Management System. Standard Field Data Sheets (FDS) are used in the EM&A program.
- 3.02 The monitoring data recorded in the equipment e.g. 1-Hour TSP meters and noise meters are downloaded directly at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data.
- 3.03 For monitoring activities which require laboratory analysis, the responsible laboratory, ALS, follows the QA/QC requirements as set out under their HOKLAS scheme for all laboratory testing.

4 ENVIRONMENTAL LICENSES AND PERMITS

4.01 Status of environmental licenses and permit is summarized in the following *Table 4-1*.

Table 4-1 Status of Environmental Licenses and Permit

Permit Type	Licenses / Permit No.	Date of Issuance by EPD	Expiry Date	Concerned Location	Status
Environmental Permit	EP-430/2011	09 July 2007	N.A.	Ping Yuen River	Valid
Notification pursuant to Section 3(1) of the Air Pollution Control Ordinance (APCO) (Construction Dust) Regulation	N.A.	N.A.	N.A.	Contract Area: Man Uk Pin, Ma Wat Wai & Ping Yuen River	Notification was made on 28 May 2012
Account for Disposal of Construction Waste	7015003	07 May 2012	N.A.	Contract Area: Man Uk Pin, Ma Wat Wai & Ping Yuen River	Valid
Application for Wastewater Discharge License under Water Pollution Control Ordinance (WPCO)	W5/1G41/1	3 October 2012	31 October 2017	Portions A, B and C near Lin Ma Hang Road, Ta Kwu Ling, N.T.	Valid
Register as a Chemical Waste Producer under Waste Disposal Ordinance	5123-642-S3565-03	3 October 2012	N.A.	3 October 2012	N.A.

SUBMISSION OF LAYOUT PLANS

4.02 Pursuant to *Clause 2.7* of EP-430/2011, 3 sets of the Layout Plans of scale 1:1000 with an explanatory statement detailing the works schedule, works boundary and the works areas have been submitted since 21 July 2012 to the Director of Environmental Protection of the HKSAR Government (hereinafter “DEP”) upon certification by the ET Leader and verification by the Independent Environmental Checker (hereinafter “the IEC”) as confirming to the information and recommendations contained in the EIA report.

SUBMISSION OF LANDSCAPE PLAN

4.03 Pursuant to *Clause 2.8* of EP-430/2011, 3 sets of the Landscape Plan have been submitted to the Director of Environmental Protection of the HKSAR Government (hereinafter “DEP”) since 21 July 2012 upon certification by the ET Leader and verification by the IEC as confirming to the information and recommendations contained in the approved EIA report.

SUBMISSION OF UPDATED ENVIRONMENTAL MONITORING AND AUDIT MANUAL

4.04 Pursuant to *Clause 2.10* of EP-430/2011, an updated environmental monitoring and audit manual for the Project, namely Updated EM&A Manual for Advanced Works under EP-430/2011 (hereinafter “the Updated EM&A Manual”), has been submitted since 21 May 2012 to the DEP upon certification by the ET Leader and verification by the Independent Environmental Checker (hereinafter “the IEC”) as confirming to the information and recommendations contained in the approved EIA report.

CONSTRUCTION ACTIVITIES

CONSTRUCTION ACTIVITIES DURING THE REPORTING PERIOD

4.05 Major construction activities of the Works undertaken during the Reporting Period are listed in **Table 4-2** below:

Table 4-2 Major Construction Activities during the Reporting Period

Portion of the Works	Major Construction Activities
Portion A Chainage R0+00 to 2+050	a. Initial survey; b. Setting out of structure /fence/gate; c. Pruning, felling and transplanting of existing trees; d. Underground utility detection; e. Liaison with various utility undertakers and villagers; and f. Laying of building layer for 31 bays; g. Construction of base slab for 20 bays; h. Construction of wall stems for 30 bays; i. Installation of drain pipe #3.
Portion B Chainage R2+050 to 2+ 838	a. Initial survey; b. Setting out of structure /fence/gate; c. Pruning, felling and transplanting of existing trees; d. Underground utility detection; e. Liaison with various utility undertakers and villagers; and f. Construction of base slab for 19 bays; g. Construction of wall stems for 16 bays; h. Temporary road diversion #5 and #6 (Filling works and road formation) i. Installation of drain pipe #9 and #10 and the associated manhole; j. Construction of box culvert #4; and k. Laying of 11kV cable by CLP.
Portion C Chainage R2+838 to 4+ 300	a. Initial survey; b. Setting out of site boundary line; c. Initial tree survey; d. Pruning, felling and transplanting of existing trees; e. Underground utility detection; f. Laying of building layer for 16 bays; g. Construction of base slab for 22 bays; h. Construction of wall stems for 3bays; and i. Excavation of retaining wall.

CONSTRUCTION ACTIVITIES DURING FORTHCOMING TWO MONTHS

4.06 Major construction activities of the Works for the forthcoming two months are listed in **Table 4-3** below:

Table 4-3 Major Construction Activities of the Works for the Forthcoming Two Months

Portion of the Works	Major Construction Activities
Portion A Chainage R0+00 to 2+050	a. Initial survey; b. Setting out of structure /fence/gate; c. Underground utility detection; d. Construction of drain pipe and box culvert; e. Construction of primary and secondary fence foundation; f. Fill between security fence footing; g. Erection of permanent security fence; h. Pruning, felling and transplanting of existing trees; i. Temporary road diversion #1 (Filling rock embankment and road formation); j. Temporary road diversion #2 (Filling works and road formation); k. Construction of deep well; and l. Construction of wheel washing facilities.
Portion B Chainage R2+050 to 2+ 838	a. Underground utility detection; b. Pruning, felling and transplanting of existing trees; c. Temporary road diversion#4, #5 and #6 (Road formation, pavement and temporary fence & EMSD cable diversion) d. Construction of drain pipe and box culvert; e. Construction of primary fence foundation and secondary fence foundation; f. Fill between security fence footing; g. Filling road and river embankment for eroded portion; h. Erection of permanent security fence; and i. Laying of 11kV cable by CLP.
Portion C Chainage R2+838 to 4+ 300	a. Setting out the site boundary line and initial survey; b. Setting out of structure /fence/gate; c. Pruning, felling and transplanting of existing trees; d. Underground utility detection; e. Construction of drain pipe; and f. Construction of primary and secondary fence foundation; and g. Construction of retaining wall.

EM&A ACTIVITIES

BASELINE MONITORING AND ESTABLISHMENT OF ENVIRONMENTAL QUALITY CRITERIA

4.07 No baseline monitoring and the associated establishment of the environmental quality criteria was conducted during the Reporting Period.

IMPACT MONITORING

4.08 No environmental monitoring was conducted during the Reporting Period.

5 WASTE MANAGEMENT

- 5.01 Pursuant to the Updated EM&A Manual, the waste management during the Reporting Period was carried out in close accordance with the Waste Management Plan, which has been submitted since 20 August 2012 to the Engineer for approval prior to commencement of the Works upon certification by the ET Leader and verification by the IEC.
- 5.02 The quantity of waste for disposal or reuse during the Reporting Period was summarized in Monthly Summary of Waste Flow Table and Disposal Records of Construction Waste in Annex K.
- 5.03 To ensure satisfactory performance of the waste management, the Contractor is reminded to comply with all relevant regulatory waste management requirements, including as appropriate those stipulated in the effluent discharge licenses and chemical waste producer registration, etc. The Contractor is also required to fully implement all the waste management mitigation measures recommended in the Updated EM&A Manual.
- 5.04 Where possible, construction materials should be reused on-site as far as practicable to reduce the construction waste, which should then be sorted or classified on site for proper recycling and disposal as recommended in the Environmental Management Plan and the associated Waste Management Plan.

6 SITE INSPECTION AND ENVIRONMENTAL AUDIT

- 6.01 Monthly site inspection and environmental audit was jointly conducted by representatives of the Engineer, IEC, ET and Contractor in close accordance with the Updated EM&A Manual.
- 6.02 During the Reporting Period, the site inspection and environmental audit was conducted on 15 November 2012.

FINDINGS/DEFICIENCIES OF THE SITE INSPECTION AND ENVIRONMENTAL AUDIT

- 6.03 Findings or deficiencies identified during the site inspection and environmental audit are summarized in *Table 6-1*.

Table 6-1 Observations of Site Inspection during the Reporting Period

Date	Findings / Deficiencies	Follow-Up Status
15 November 2012	Excavation activities were undertaken within Portion C. Watering was observed during construction activities. Wheel washing machine was also observed functioning well. No adverse environmental impacts were found. Full implementation of the required environmental mitigation measures is reminded, in particular construction dust suppression measures during dry season throughout the whole Project area.	Not required for general reminders

- 6.04 Site inspection checklists completed and endorsed by all related parties are kept by the ET and are available for inspection upon request.

DISCUSSION AND CONCLUSION

- 6.05 No deficiencies and non-compliance with the relevant regulatory requirements were identified during the regular site inspection and environmental audit, indicating no adverse environmental impacts were generated from the construction of the Works.

RECOMMENDATION

- 6.06 Although no adverse environmental impacts were identified during the regular site inspection and environmental audit conducted by representatives of the Engineer, IEC, ET and Contractor, full implementation of the recommended environmental mitigation measures, particularly construction dust suppression measures e.g. watering during dusty activities under dry and windy conditions, as well as sedimentation of the site run off during rainy conditions, are reminded.

7 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

7.01 No environmental complaint was received during the Reporting Period. Summary of environmental complaint is presented in **Table 7-1** below.

Table 7-1 Summary of Environmental Complaints

Reporting Month	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
August to October 2012	0	0	Not Applicable
November 2012	0	0	Not Applicable

7.02 No summons and prosecution was received during the Reporting Period. Summary of summon and prosecution is presented in **Table 7-2** and **Table 7-3** below.

Table 7-2 Summary of Environmental Summons

Reporting Month	Environmental Summons Statistics		
	Frequency	Cumulative	Nature
August to October 2012	0	0	Not Applicable
November 2012	0	0	Not Applicable

Table 7-3 Summary of Environmental Prosecution

Reporting Month	Environmental Prosecution Statistics		
	Frequency	Cumulative	Nature
August to October 2012	0	0	Not Applicable
November 2012	0	0	Not Applicable

8 IMPACT FORECAST

KEY ENVIRONMENTAL ISSUES

8.01 Potential environmental issues to be considered in the coming month include:-

- (a) Air quality In dry season under dry and windy conditions, dusty construction activities may generate potential construction dust impacts and dry/loose/exposure soil surface/stock piles of dusty material within the site may pose fugitive dust under dry and windy weather conditions;
- (b) Water quality In wet season, surface runoff during heavy storm/rain may pollute the surrounding water bodies with high suspended solids or turbidity, and concrete washing may increase alkalinity or pH value of the water bodies;
- (c) Chemical waste Oil & grease spillage or leakage from construction equipment and the associated oil containers within site areas may contaminate lands or other environment;
- (d) Construction Noise Construction noise impacts may be caused from noisy construction activities;

ENVIRONMENTAL MITIGATION MEASURES FOR THE COMING MONTH

- 8.02 Environmental Mitigation Measures to be considered in the coming month includes:-
- (a) Dust suppression measures, in particular proper watering during dusty construction activities under dry and dusty conditions, should be fully implemented;
 - (b) Sedimentation or silt removal facilities of adequate capacity should be used, for proper treatment of any site effluent generated from stockpiles of construction materials/waste or dusty haul roads or excavated surfaces within the site during storm rain, prior to discharge to nearby water bodies in order to remove suspended solids or turbidity;
 - (c) Good management of chemical wastes should be maintained;
 - (d) Follow-up actions for any defects identified during regular site inspection should be promptly taken to rectify the situation; and
 - (e) As high noise levels were sometimes recorded during the Reporting Period, special attention is drawn to implementation of the construction noise mitigation measures during noisy construction works.

9 CONCLUSIONS AND RECOMMENDATIONS

CONCLUSIONS

- 9.01 No environmental monitoring is conducted during the Reporting Period.
- 9.02 No non-compliance with the regulatory requirements was recorded in the IEC and ET regular site inspection and environmental audit jointly conducted by representatives of the Engineer, IEC, ET and Contractor during the Reporting Period, indicating no adverse environmental impacts were generated from construction activities under the Works during the Reporting Period.
- 9.03 Defects of minor environmental significance were sometimes observed. The identified defects were normally rectified on site or within the specified time prior to the next site inspection.
- 9.04 No environmental complaint, notification of summons or successful prosecution was registered during the Reporting Period.

RECOMMENDATION

- 9.05 The Contractor is reminded to fully comply with all the relevant regulatory environmental requirements, including environmental mitigation measures stipulated in all the environmental ordinances, EM&A Manual, EMP and the associated WMP, effluent discharge license and the chemical waste producer registration, etc.
- 9.06 Attention is drawn to implementation of air quality mitigation measures, in particular construction dust suppression measures during dusty construction activities under dry and windy conditions.
- 9.07 In addition, full implementation of the required water quality mitigation measures is reminded to eliminate adverse water quality impacts generated from site water runoff, surfaces of haul roads, stock pile of excavated materials, etc.
- 9.08 Attention is also drawn to implementation of the construction noise mitigation measures during noisy construction works.

ANNEX A

LOCATION PLAN FOR THE WORKS

Key

 Project Area

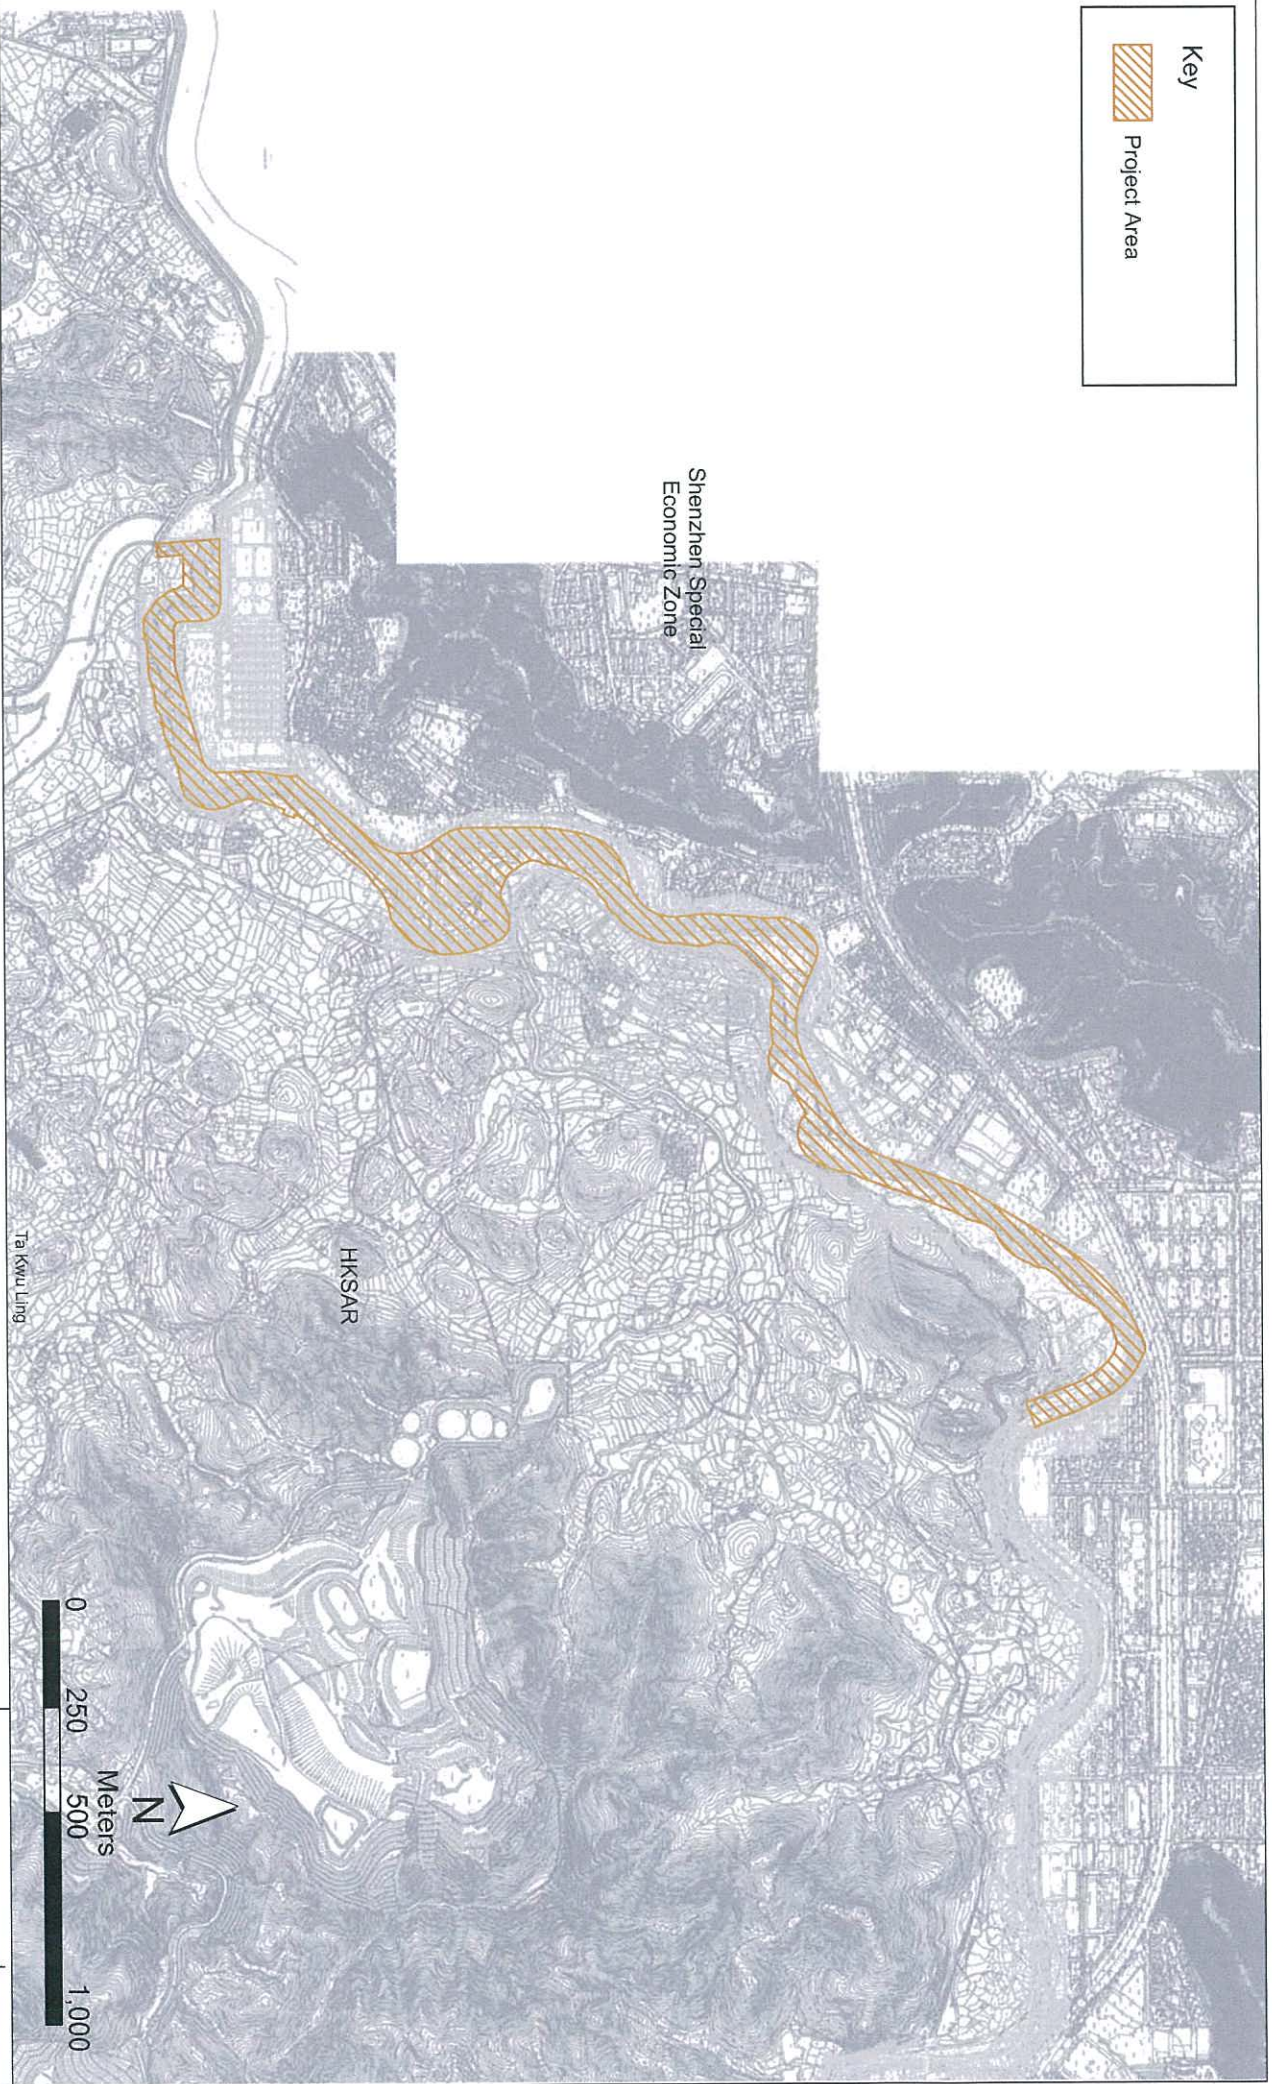


Figure A1-1

Location of Project Site

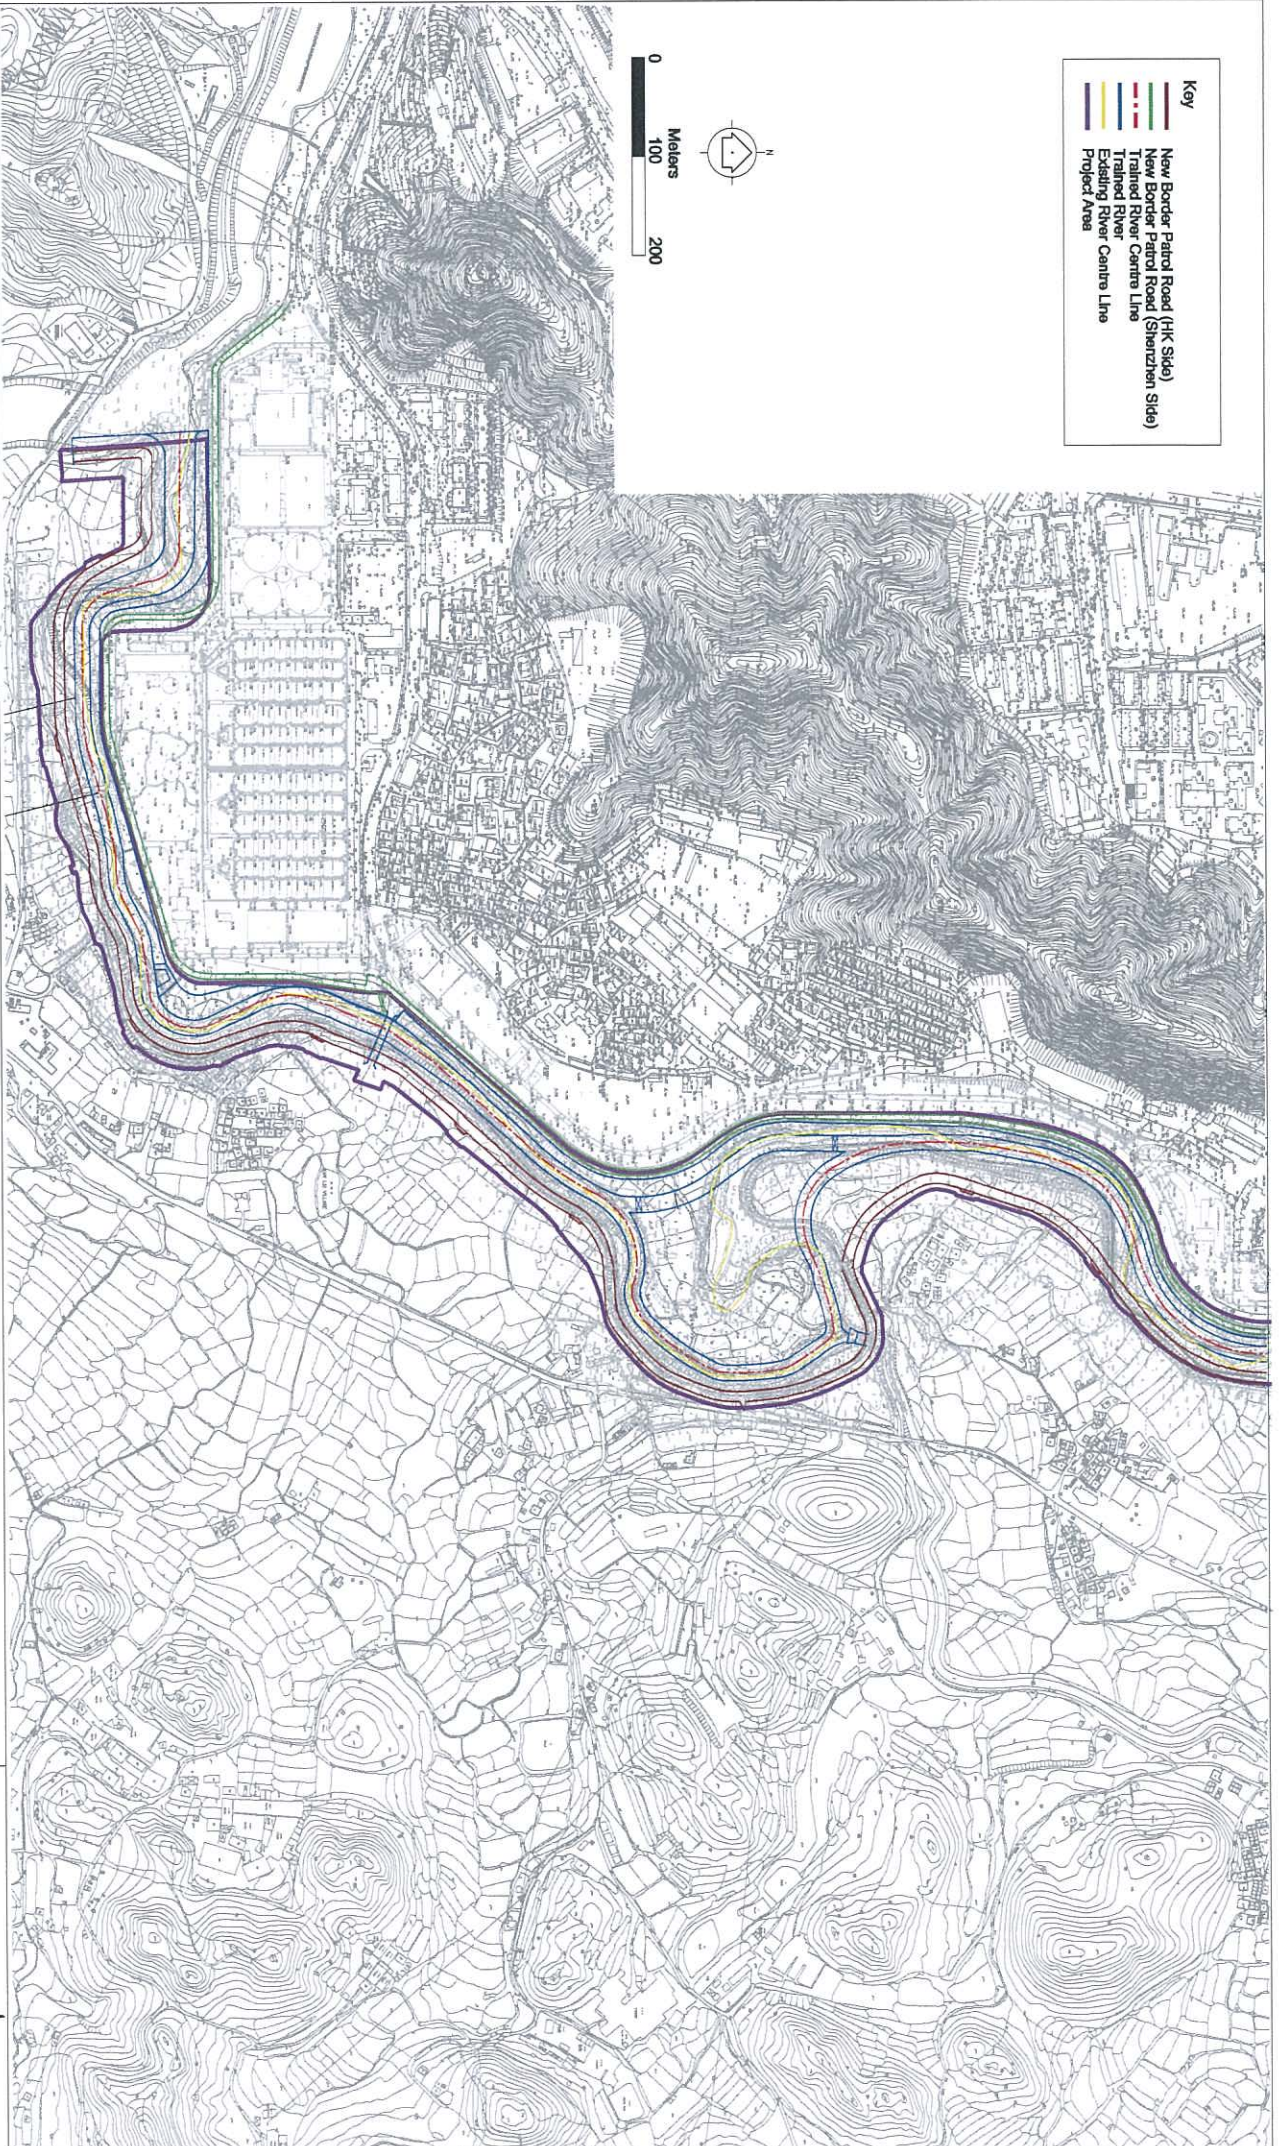


Figure A1-2

General Layout and Extent of the Trained River
(1 of 2)


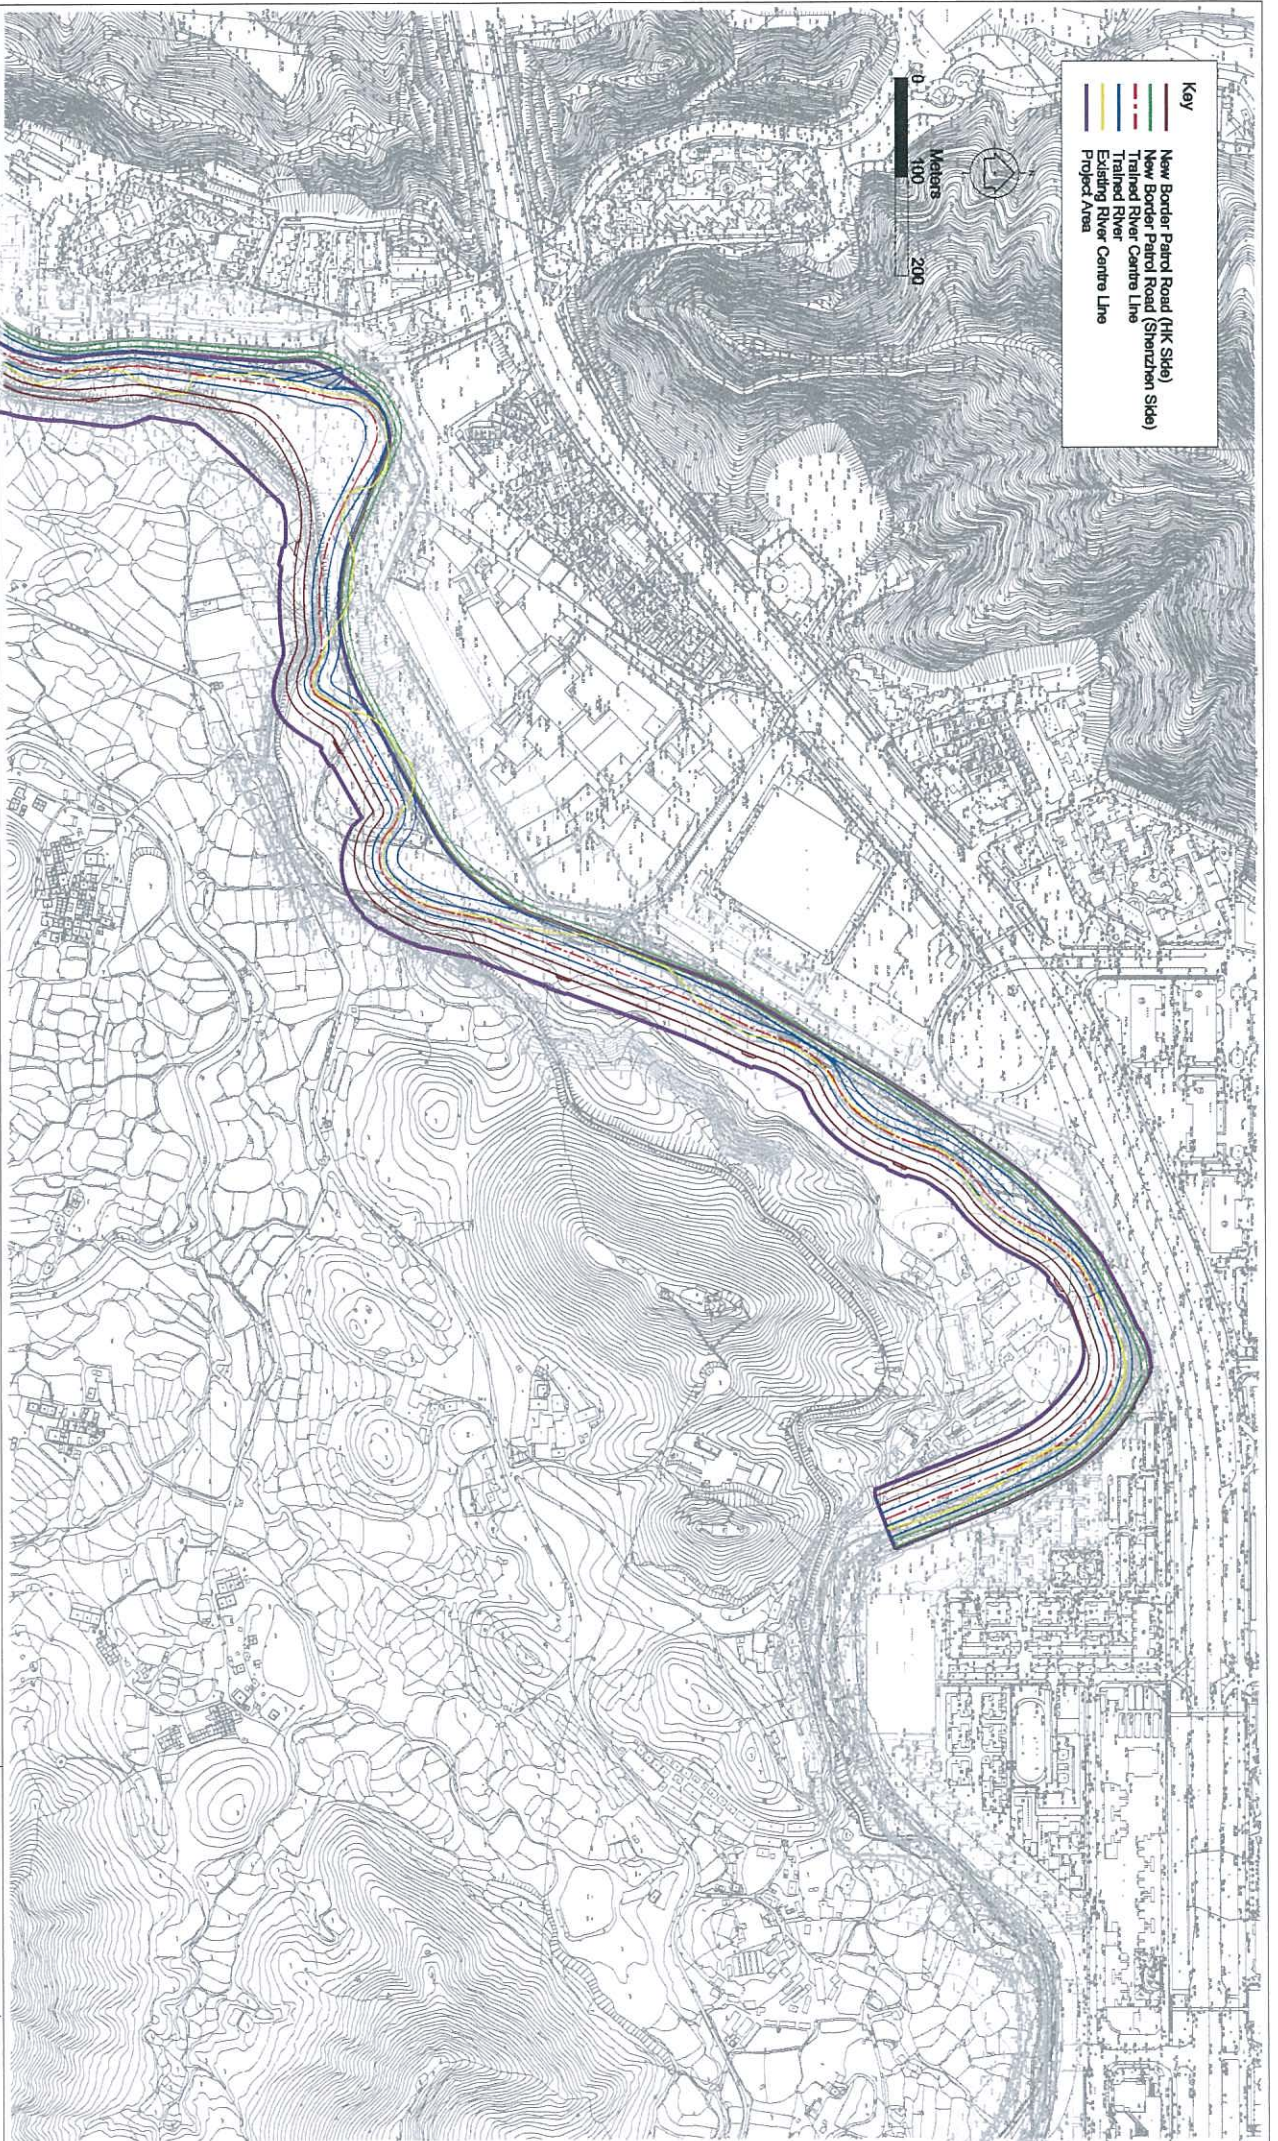



Figure A1-2

General Layout and Extent of the Trained River
(2 of 2)

FILE: 0101726M1-3.dwg
DATE: 23/10/2009



KEY PLAN
SCALE 1 : 50000

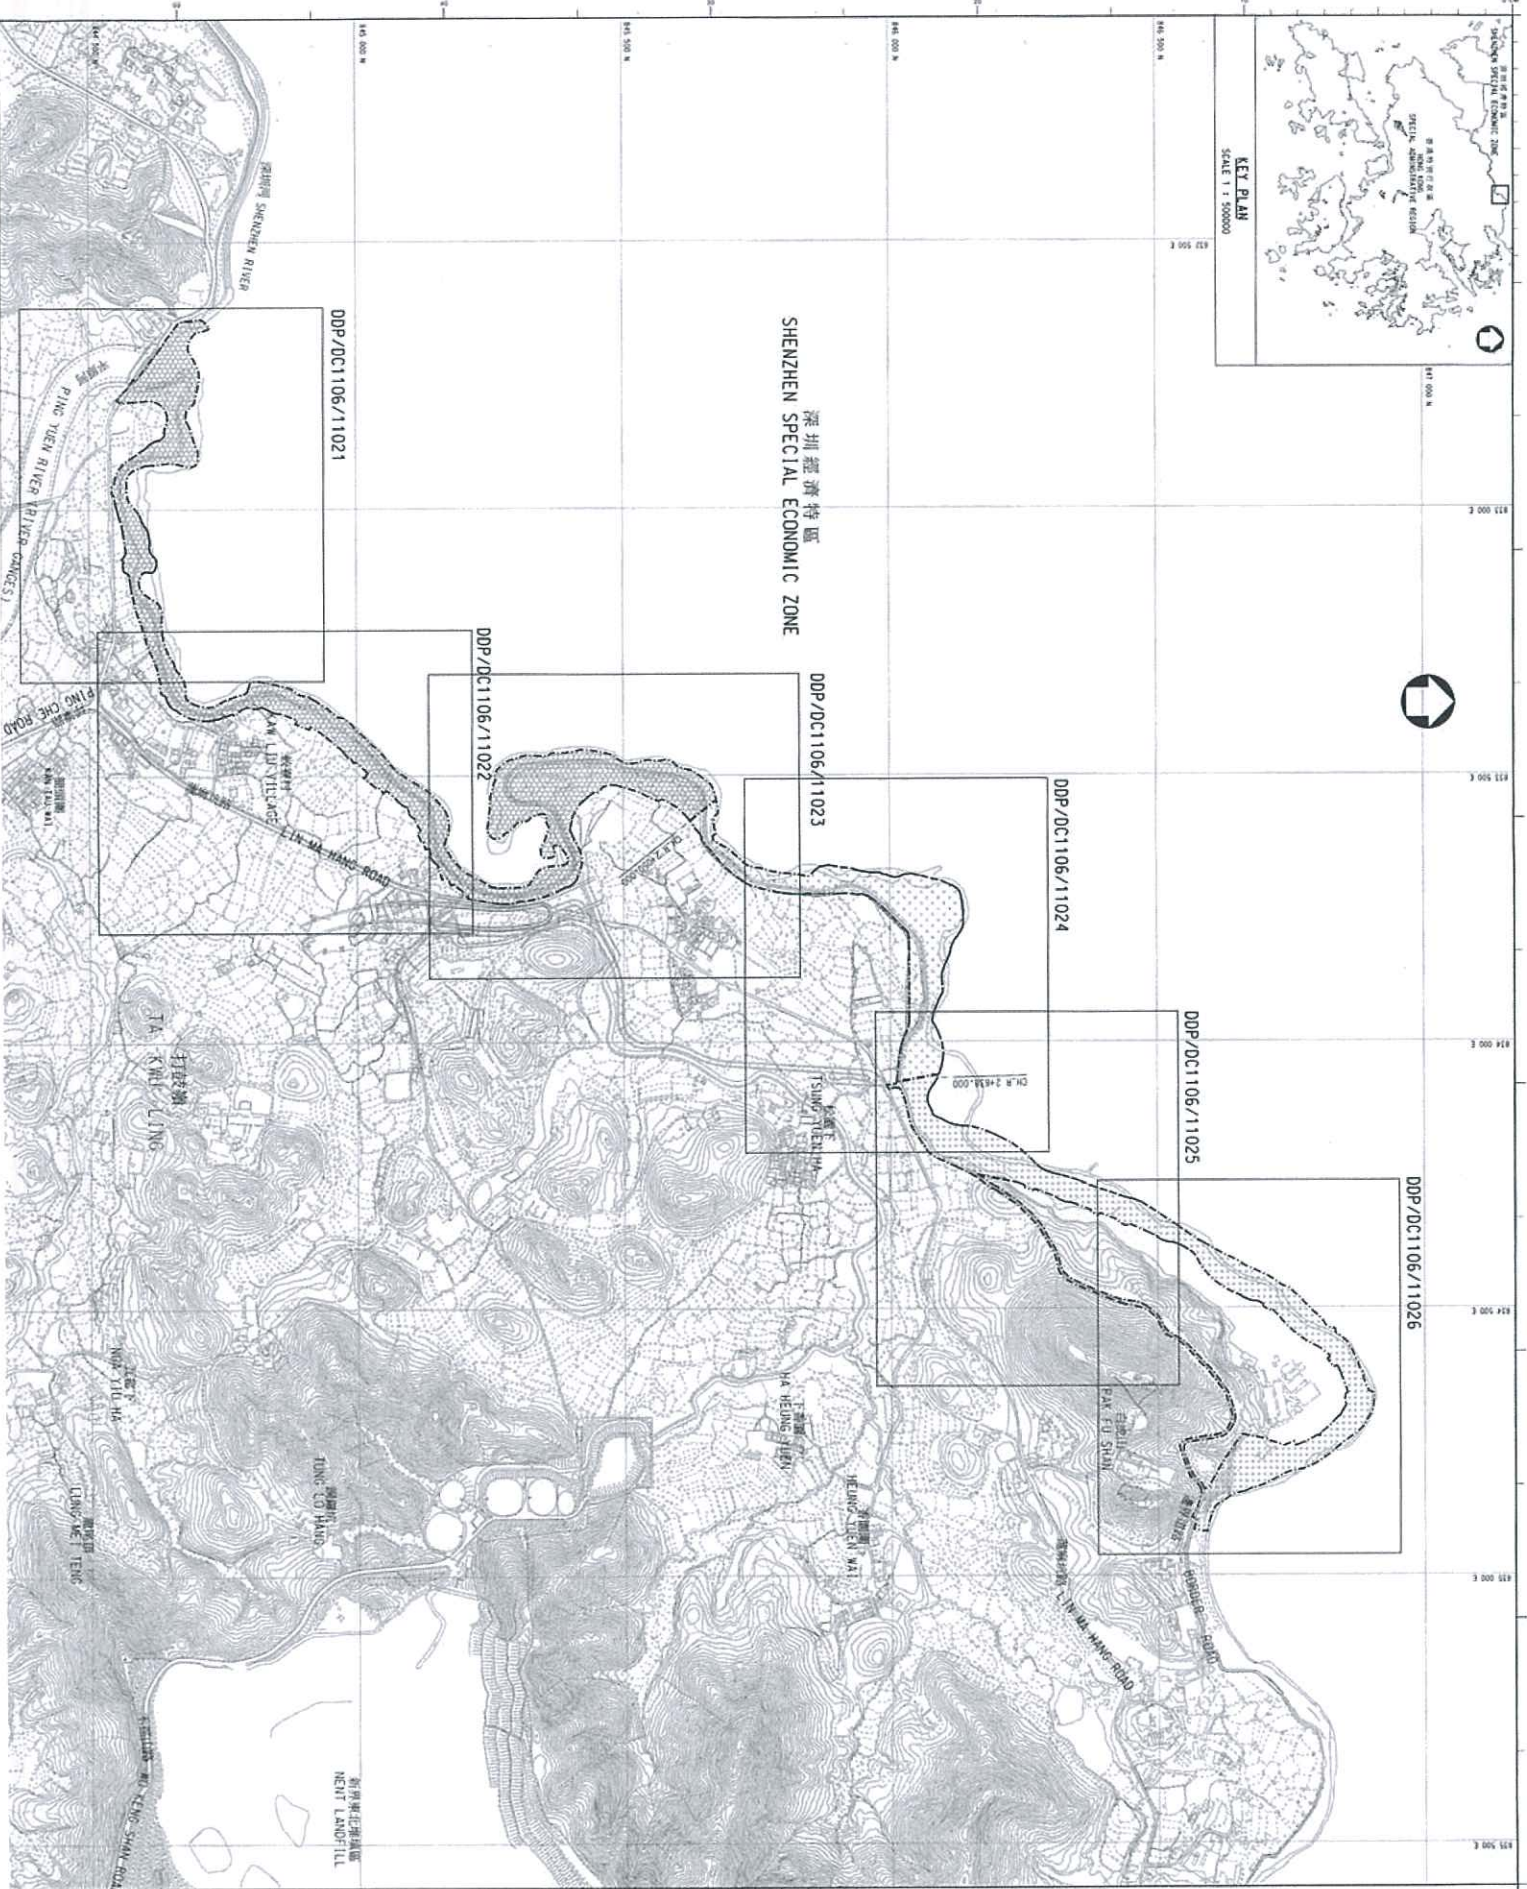

DDP/DC1106/11026

DDP/DC1106/11025

DDP/DC1106/11024

DDP/DC1106/11023

DDP/DC1106/11022

DDP/DC1106/11021


NOTES:

1. GRID LINES ARE HONG KONG GRID 1980.
2. ALL LEVELS ARE IN METRES AND REFERRED TO M.S.L.
3. FOR SETTING OUT DETAILS OF SITE LIMIT TO REFER TO DRAWING NO. DDP/DC1106/11011 TO DDP/DC1106/11021.
4. FOR DETAILS OF AREAS B1, B2 B3 & B4 REFER TO DRAWING NO. DDP/DC1106/11022.

LEGEND:

- LIMIT OF THE SITE
 - ▨ PROTION A
 - ▨ PROTION B
 - ▨ AREA B1
 - ▨ AREA B2
 - ▨ AREA B3
 - ▨ AREA B4
 - ▨ PROTION C
- DATA SOURCE: CADASTRE FOR HONG KONG

NO.	DATE	DESCRIPTION	BY
1	28 NOV 2011	DESIGNED	K. K. LI
2	28 NOV 2011	DRAWN	S. K. LUI
3	28 NOV 2011	CHECKED	M. H. HOON
4	28 NOV 2011	VALIDATED	L. C. LAU

APPROVED: 
K. K. LI
Ag. Chief Engineer
Date: 28 NOV 2011

contract no. DC/2011/06
the no. DP/8/501868
project no. 501868
contract

REPRODUCTION OF BOUNDARY PATROL ROAD AND ASSOCIATED SECURITY FACILITIES BETWEEN PING TSEW RIVER AND PARK FU SHAN AND DRAINAGE WORKS IN NORTH DISTRICT


SCOPE OF WORKS AT PORTION A, B AND C OF THE SITE


SHEET 1 OF 21
drawing no. DDP/DC1106/11011
scale 1 : 5 000

COPYRIGHT RESERVED

DRAINAGE PROJECTS DIVISION


DRAINAGE SERVICES DEPARTMENT
GOVERNMENT OF THE HONG KONG SPECIAL ADMINISTRATIVE REGION



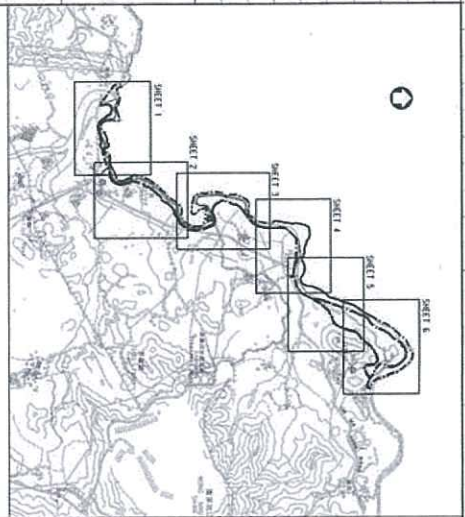

LOCATION PLAN
SCALE 1:20000

深圳市
SHENZHEN SHI

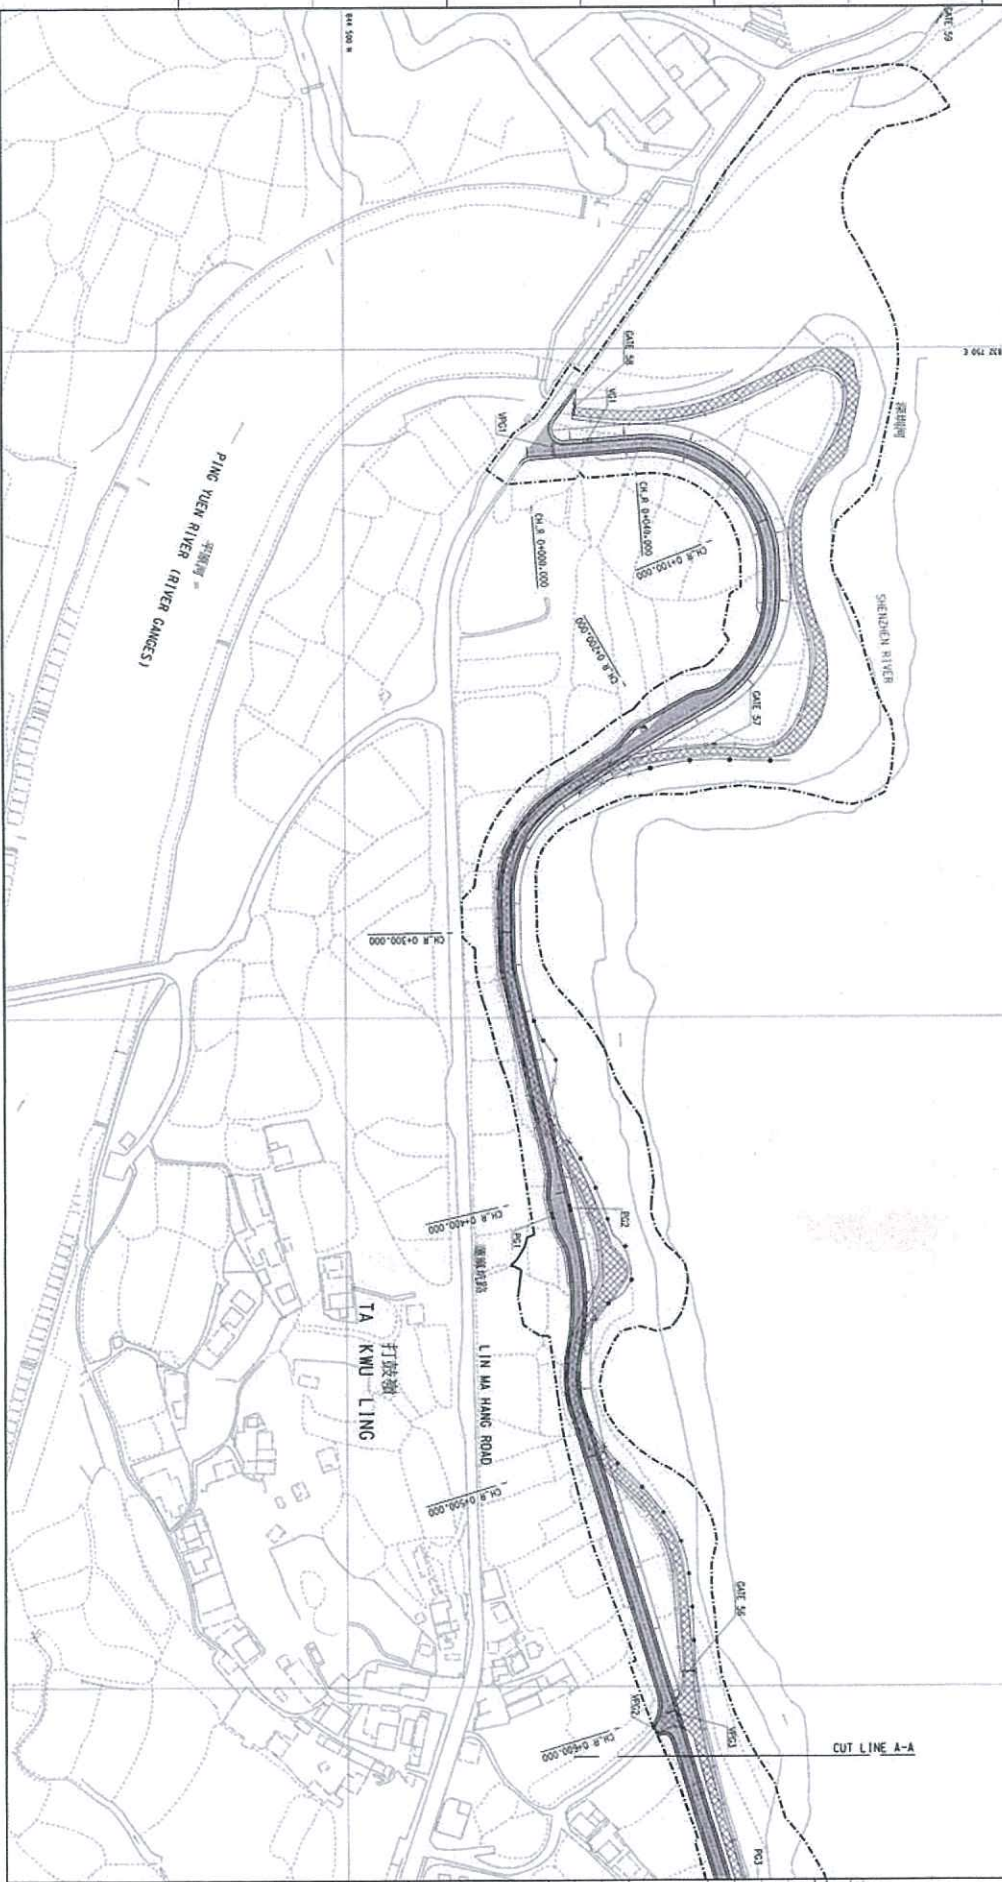

REPRODUCTION OF BOUNDARY PATROL ROAD AND ASSOCIATED SECURITY FACILITIES BETWEEN PING YUEN RIVER AND PAK FU SHAN AND DRAINAGE WORKS IN NORTH DISTRICT

Project no. 501808

Contract no. DC/2011/06

File no. DP/8/501808

Contractor: K. Y. Tong & Co. Ltd.

Design: C. I. CHAN, 28 Nov 2011

Checked: W. H. NG, 28 Nov 2011

Approved: S. C. LAU, 28 Nov 2011

Scale: 1:1000

Drawing no. DDP/DC/1106/11021

Sheet 1 of 51

Office: DRAINAGE SERVICES DEPARTMENT, GOVERNMENT OF THE HONG KONG SPECIAL ADMINISTRATIVE REGION

Copyright Reserved

DRAINAGE PROJECTS DIVISION

NOTES:


1. CHAIN LINKS ARE HONG KONG GRID 1980.
2. ALL LENGTHS ARE IN METRES AND REFERRED TO IN METRES.

LEGEND:

- LIMIT OF THE SITE
- EXISTING BOUNDARY PATROL ROAD
- EXISTING BOUNDARY PATROL ROAD TO BE RECONSTRUCTED
- PROPOSED BOUNDARY PATROL ROAD
- PROPOSED PAK FU SHAN PRIMARY BOUNDARY FENCE
- PROPOSED PAK FU SHAN SECONDARY BOUNDARY FENCE
- EXISTING BOUNDARY FENCE AND ASSOCIATED LAMP POST AND PILLAR BOX
- EXISTING BOUNDARY FENCE AND ASSOCIATED LAMP POST AND PILLAR BOX TO BE DEMOLISHED
- PROPOSED PAK FU SHAN PRIMARY BOUNDARY FENCE TO BE DEMOLISHED
- EXISTING CHAIN LINK FENCE TO BE DEMOLISHED
- EXISTING CHAIN LINK FENCE TO BE RECONSTRUCTED
- PROPOSED CUT SLOPE
- PROPOSED FILL SLOPE
- CH. 8 THROUGH CHAINAGE FROM BOUNDARY ROAD
- PROPOSED VERGEE AS AND RESTRICTION GATE (V.R.G.)
- PROPOSED RESTRICTION GATE (R.G.)
- EXISTING GATE
- EXISTING GATE TO BE DEMOLISHED
- PILLAR BOX
- SWITCH ROOM

REVISION:

NO.	DATE	DESCRIPTION	INITIAL
1	28 Nov 2011	DESIGNED	C. I. CHAN
2	28 Nov 2011	CHECKED	W. H. NG
3	28 Nov 2011	APPROVED	S. C. LAU

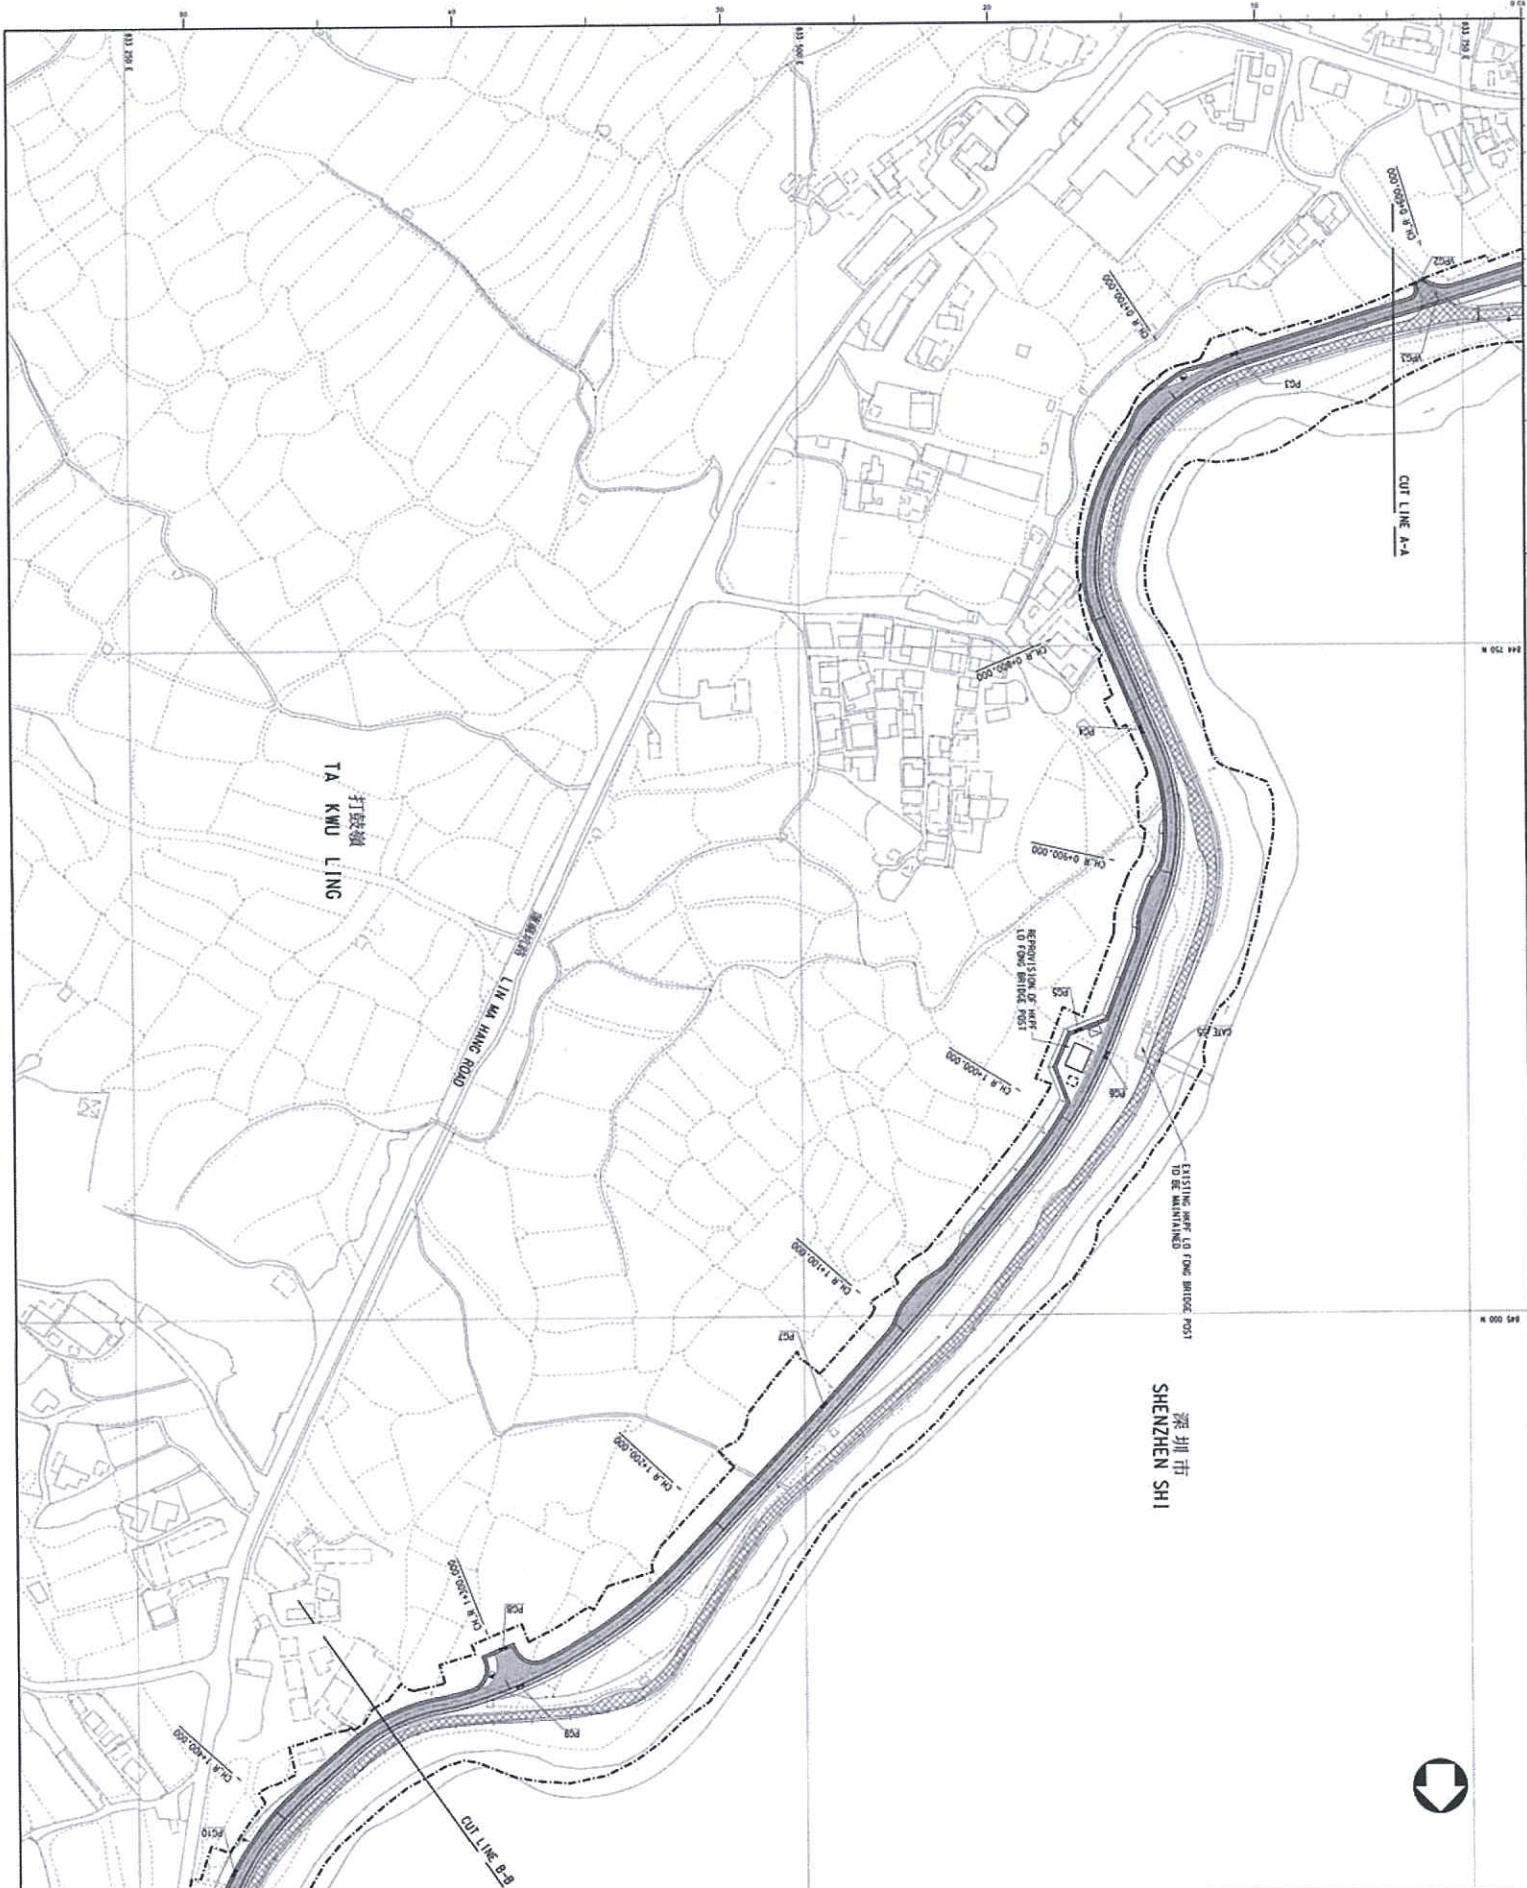

NOTES:
1. FOR GENERAL NOTES & LEGEND, REFER TO DRG. NO. DS/2011/001.

NO.	DATE	DESCRIPTION	INITIALS
1	28 NOV 2011	DESIGN	
2	28 NOV 2011	DESIGN	
3	28 NOV 2011	DESIGN	
4	28 NOV 2011	DESIGN	
5	28 NOV 2011	DESIGN	
6	28 NOV 2011	DESIGN	
7	28 NOV 2011	DESIGN	
8	28 NOV 2011	DESIGN	
9	28 NOV 2011	DESIGN	
10	28 NOV 2011	DESIGN	

Ag. Chief Engineer
S. L. LING
28 NOV 2011
12:50

contract no. DC/2011/05
file no. DP/8/5018C8
project no. 5018C8

REPROVISIONING OF BOUNDARY PATROL ROAD AND ASSOCIATED SECURITY FACILITIES BETWEEN PING TIEN RIVER AND PAK HOI AND DRAINAGE WORKS IN NORTH DISTRICT


drawing title
GENERAL LAYOUT

(SHEET 2 OF 5)

drawing no. DDP/DC1106/11022
scale 1:1,000

office
DRAINAGE PROJECTS DIVISION
DRAINAGE SERVICES DEPARTMENT
GOVERNMENT OF THE
HONG KONG
SPECIAL ADMINISTRATIVE REGION

COPYRIGHT RESERVED





NOTES:
 1. FOR GENERAL NOTES & LEGEND, REFER TO Dwg. No. DP/DC1106/11023.


NO.	DATE	DESCRIPTION	INITIAL
DESIGNED	28 NOV 2011		
DRAWN	28 NOV 2011		
CHECKED	28 NOV 2011		
VERIFIED	28 NOV 2011		
APPROVED	28 NOV 2011		

As Chief Engineer
 DATE

REPRODUCTION OF BOUNDARY PATROL ROAD AND ASSOCIATED SECURITY FACILITIES BETWEEN PING TUN RIVER AND PAK FU SHAN AND DRAINAGE WORKS IN NORTH DISTRICT

drawing title
GENERAL LAYOUT
 SHEET 3 OF 51
 drawing no.
DDP/DC1106/11023
 scale
 1 : 1 000

office
COPYRIGHT RESERVED
DRAINAGE PROJECTS DIVISION
 DRAINAGE SERVICES DEPARTMENT
 GOVERNMENT OF THE
 HONG KONG
 SPECIAL ADMINISTRATIVE REGION

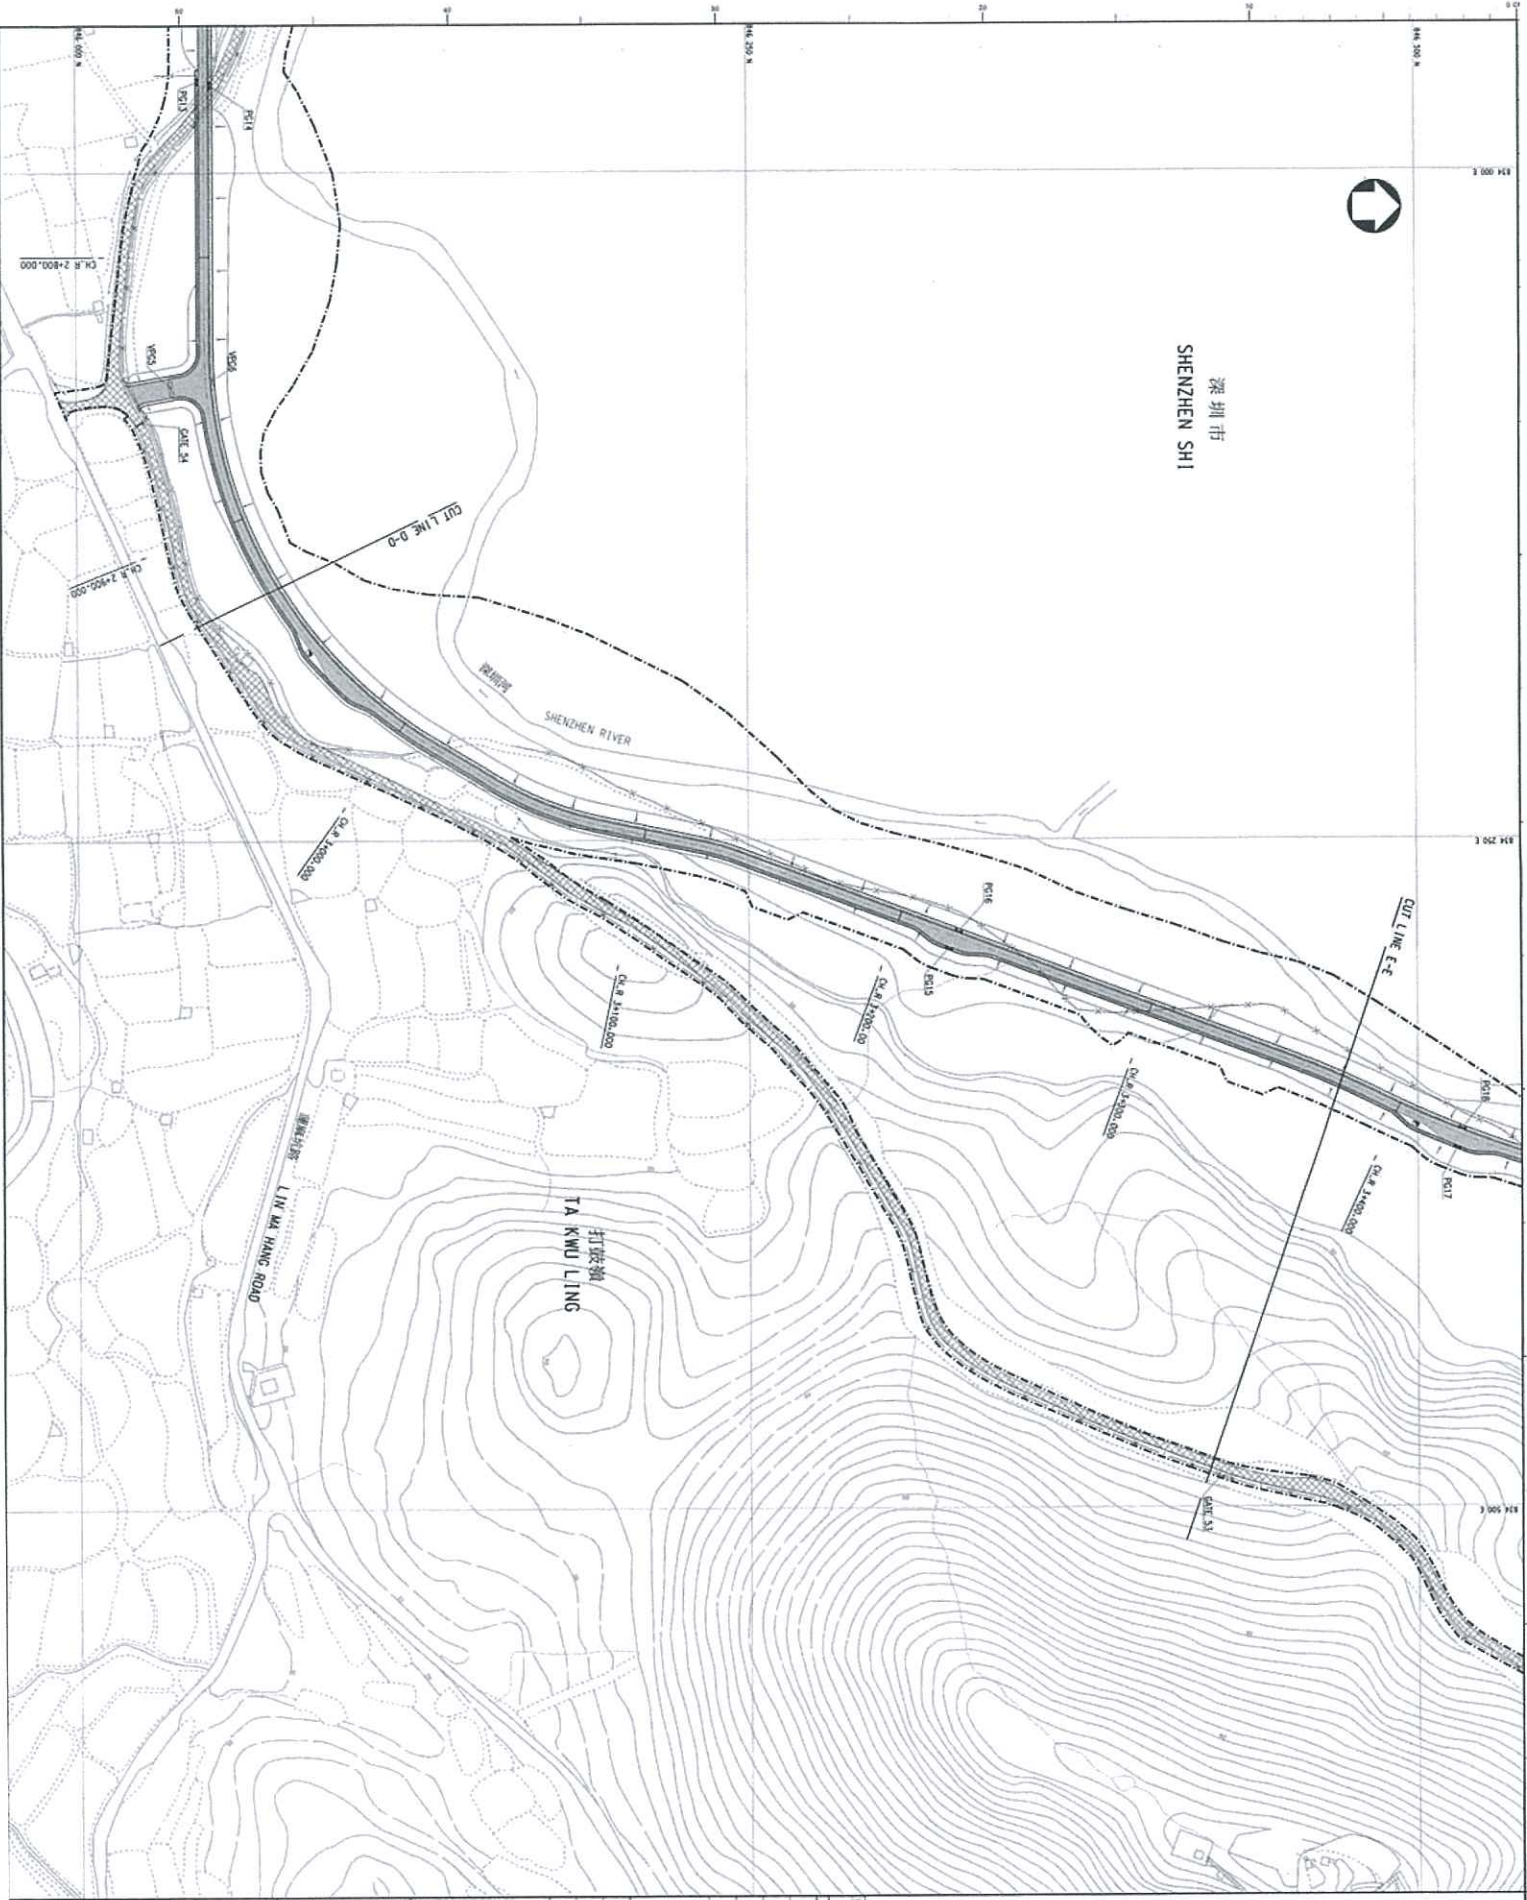

深圳市
SHENZHEN SHI

NOTES:
1. FOR GENERAL NOTES & LEGEND, REFER TO
DPP, NO. DP/DC/1106/1102/1.

NO.	DATE	DESCRIPTION	INITIAL
1			

DESIGNED: C. F. CHAN 24 NOV 2011
 DRAWN: T. M. LEE 24 NOV 2011
 CHECKED: W. H. NG 24 NOV 2011
 VERIFIED: L. L. YAU 24 NOV 2011
 APPROVED: [Signature] 24 NOV 2011

Ag. Chief Engineer
 Contract no. DC/2011/05
 File no. DP/8/501808
 Project no. 501808

REPROVISIONING OF BOUNDARY PATROL ROAD
 AND ASSOCIATED SECURITY FACILITIES
 BETWEEN PING TIER RIVER
 AND PAK FU SHAN AND DRAINAGE WORKS
 IN NORTH DISTRICT

drawing title
GENERAL LAYOUT


(SHEET 5 OF 6)
 drawing no. DDP/DC/1106/11025
 scale 1:1,000

COPYRIGHT RESERVED
DRAINAGE PROJECTS DIVISION





深圳市
SHENZHEN SHI

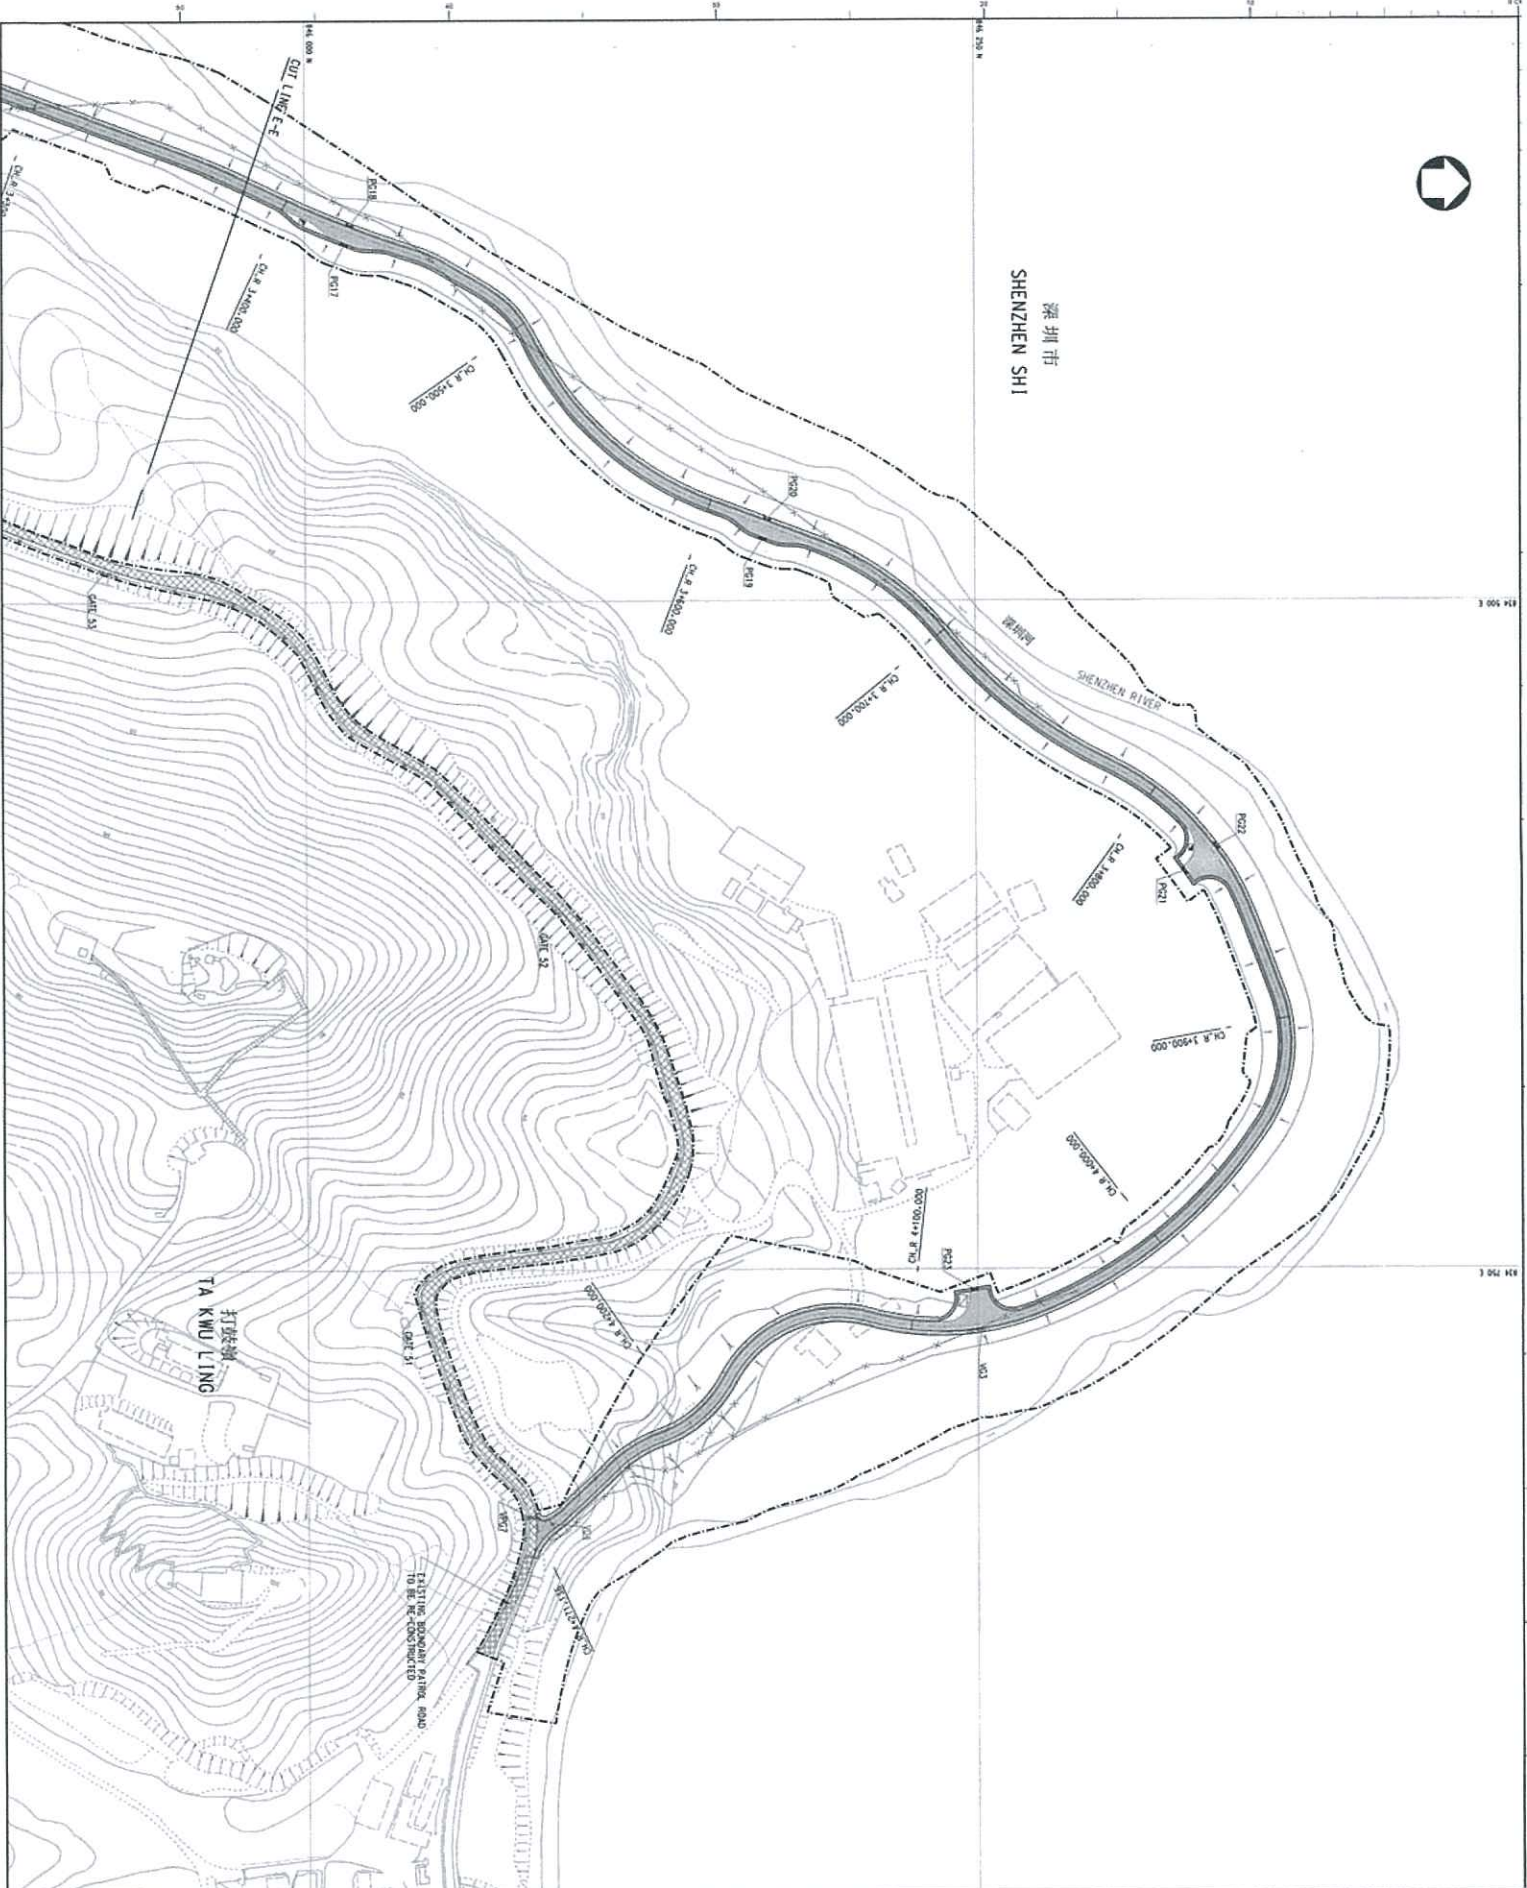

NOTES:
1. FOR GENERAL NOTES & LEGEND, REFER TO
DRAWING NO. DDP/DC/1106/1102/1.

NO.	DATE	DESCRIPTION	INITIAL
REVISION			
1		DESIGNED	
2		DRAWN	
3		CHECKED	
4		APPROVED	

Ag. Chief Engineer

 28 NOV 2011
 DATE

contract no. DC/2011/06
 H/S no. DP/8/501808
 project no. 501808
 contract


REPROVISIONING OF BOUNDARY PATROL ROAD
 AND ASSOCIATED SECURITY FACILITIES
 BETWEEN PING VIEN RIVER
 AND PAK TU SHAN AND DRAINAGE WORKS
 IN NORTH DISTRICT

drawing title
GENERAL LAYOUT

SHEET 6 OF 61
 drawing no. DDP/DC/1106/11026
 scale 1:1,000


COPYRIGHT RESERVED

DRAINAGE PROJECTS DIVISION



ANNEX B

***ENVIRONMENTAL MANAGEMENT ORGANIZATION
AND COMMUNICATION LINES***

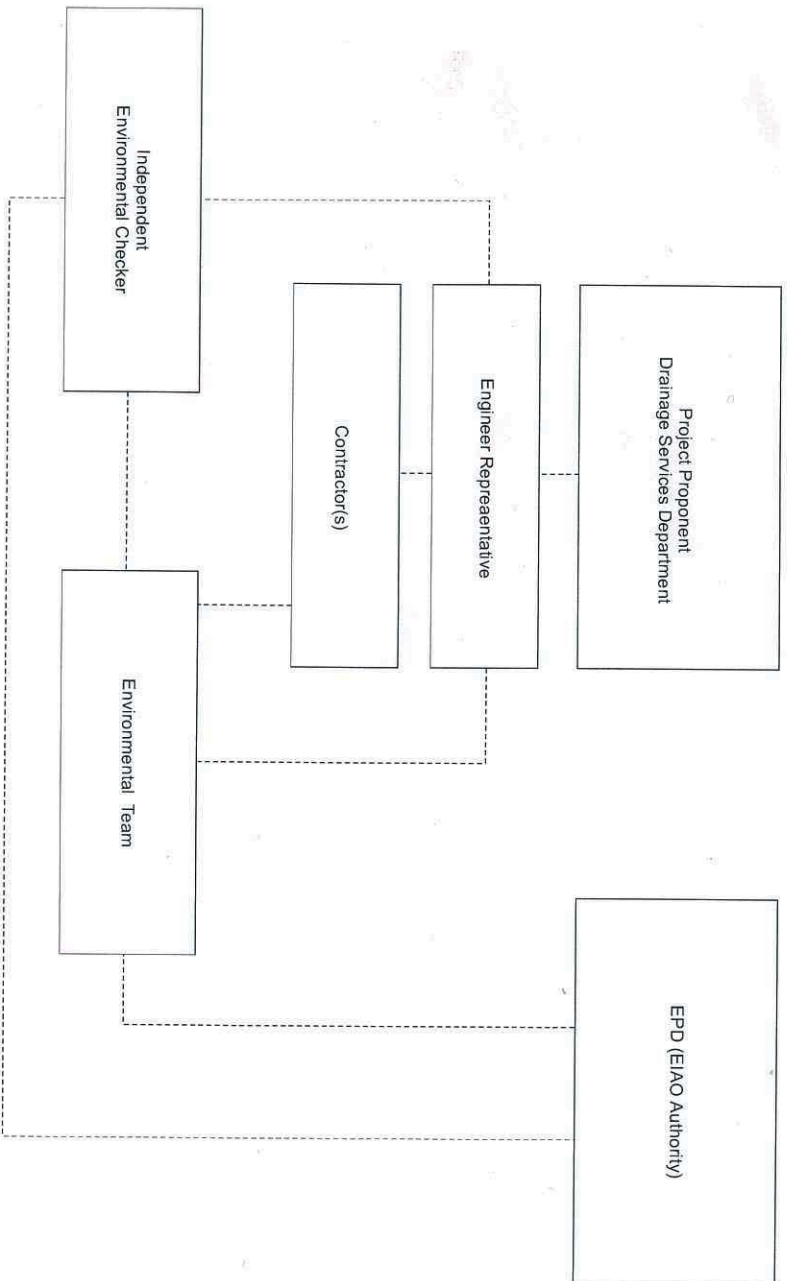

Key
----- Line of Communication

EM&A Organisation Chart

KEY CONTACT INFORMATION UNDER THE CONTRACT

Contact Details of Key Personnel

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
DSD	Project Proponent / Employer	Mr. Eric Y. M. Cheng	2594-7341	2827-8700
Environ	Independent Environmental Checker	Mr. Roger W. K. Leung	3743-0754	3548-6988
CHCC	Project Manager	Mr. Raymond Yau	2403 1165	2403 1165
SHCC	Site Agent	Mr. Elvin Lam	2640 9286	2640 9286
AUES	Environmental Team Leader	Mr. T. W. Tam	2959-6059	2959-6079
AUES	Senior Environmental Consultant	Mr. Wong Fu Nam	2959-6059	2959-6079
AUES	Environmental Team Supervisor	Mr. Ben Tam	2959-6059	2959-6079

Project Proponents' Contact Numbers

Project Proponent	The Engineer	Telephone Number	Fax Number	24-Hour Hotline
DSD	Mr. Eric Y. M. Cheng	2594 7450	2594 7341	6770 3827

24-Hour Hotline Telephone Number for the Public to Make Enquiries

24-Hour Hotline
6770 3827

Legends:

DSD (Project Proponent / Engineer) – Drainage Services Department

SHCC (Main Contractor) – Sang Hing Civil Constructors Co., Ltd

Environ (IEC) – Environ Hong Kong Limited

AUES (ET) – Action-United Environmental Services & Consulting

ANNEX C

IMPLEMENTATION SCHEDULE

FOR ENVIRONMENTAL MITIGATION MEASURES

Annex D Implementation Schedule for Environmental Protection Measures

EIA Ref.	Environmental Protection Measures	Location/Duration of Measures/Timing of Completion of Measures	Implementati on Agent	Implementation Stage			Relevant Legislation & Guidelines
				Des C	Post-C	O	
1. Air Quality							
S4.8	<p>Dust control measures stipulated in the <i>Air Pollution Control (Construction Dust) Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions. In particular:</p> <ol style="list-style-type: none"> i. Water spraying on haul roads and dusty areas for every hour during construction; ii. Covering the stockpile areas of at least 70% area with tarpaulin sheet or impervious sheet; iii. Covering of dusty materials/spoils on trucks by impervious sheets; iv. Controlling the dropping height of fill materials; v. Covering or storing all debris and materials in a sheltered debris collection area; vi. Storing dredged sediment in a separate enclosed tank; and vii. Providing wheel washing facility at each exit of the works site. 	Whole Site / During Construction	Contractor	✓			Air Pollution Control (Construction Dust) Regulation
S4.8	Site practices such as regular maintenance and checking of the diesel powered mechanical equipment will be adopted to avoid any black smoke emissions and to minimize gaseous emissions.	Whole Site / During Construction	Contractor	✓			
2. Construction Noise							
S5.8	<p>The following site practices should be followed during the construction of the Project:</p> <ol style="list-style-type: none"> i. Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction phase; ii. Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction phase; iii. Mobile plant, if any, should be sited as far from NSRs as possible; iv. Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; v. Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and vi. Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 	Whole Site / During Construction	Contractor	✓			
S5.8	Use quiet PME as far as practicable to mitigate the construction noise impacts.	Whole Site / During Construction	Contractor	✓			
S5.8	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. With reference to A Practical Guide for the Reduction of Noise from Construction Works, the noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.	Works Area III and IV/ During Construction	Contractor	✓			A Practical Guide for the Reduction of Noise from Construction Works

S5.8	Scheduling of construction activities with identified grouping of PMEs.	Works Area III / During Construction	Contractor	✓			
S5.10	Monthly site inspection and audit of construction activities.	Whole Site / During Construction	ET & IEC	✓			EIAO
3. Water Quality							
S6.8	Maximum loss rate during the wet excavation should be kept at or below the limits specified in the EIA Report.	Excavation area / During Construction	Contractor	✓			
S6.8	<i>Construction Site Runoff and Drainage</i> Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in Appendix A1 of ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Land Site / During Construction	Contractor	✓			ProPECC PN 1/94 TM standard under the WPCO
S6.8	Non-active area along the river bank will be covered by impermeable sheets or hydroseeding completed sections immediately whenever possible to minimise erosion of soil by runoff particularly during heavy rainstorms	River bank / During Construction	Contractor	✓			
S6.8	Earthworks to form the final surfaces will be followed up with surface protection and drainage works to prevent erosion caused by rainstorms.	Land Site / During Construction	Contractor	✓			
S6.8	Appropriate surface drainage will be designed and provided where necessary. In particular, surface runoff will be collected along the river bank and be diverted to sedimentation tank/pond before being discharged into the river.	Land Site / During Construction	Contractor	✓			
S6.8	The precautions to be taken at any time of year when rainstorms are likely together with the actions to be taken when a rainstorm is imminent or forecasted and actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94.	Land Site / During Construction	Contractor	✓			ProPECC PN 1/94 TM
S6.8	Oil interceptors will be provided in the drainage system where necessary and regularly emptied to prevent the release of oil and grease into the storm water drainage system after accidental spillages.	Land Site / During Construction	Contractor	✓			
S6.8	Temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of storm flows	Land Site / During Construction	Contractor	✓			
S6.8	The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or when the temporary diversion is no longer required.	Land Site / During Construction	Contractor	✓			
S6.8	An adequate number of portable toilets will be provided for the on-site construction workforce. Wastewater/sewage will be handled by registered collector in Hong Kong.	Whole Site / During Construction	Contractor	✓			
S6.8	Debris and refuse generated on-site will be collected, handled and disposed of properly to avoid entering the nearby WSRs. Stockpiles of cement and other construction materials will be covered when not being used.	Whole Site / During Construction	Contractor	✓			
S6.8	Oil leakage or spillage will be contained and clean up immediately. Waste oil will be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance.	Whole Site / During Construction	Contractor	✓			Waste Disposal Ordinance

4. Terrestrial Ecology									
S7.11	Avoid potential impacts on the trees whenever possible during the detailed design stage. The retained trees will be fenced off as protection from the construction works. If the trees cannot be avoided due to the engineering constraint, the affected individual(s) will be transplanted to compensatory woodland planting site near Pak Fu Shan or a similar habitat in the vicinity of the Project Site if considered suitable (subject to the detailed assessment of the feasibility of transplantation).	Whole Site / During Construction	Contractor	✓	✓				
S7.11	A detailed vegetation survey on the trees within the impacted area would be conducted by a suitably qualified botanist/ ecologist to identify and record the affected individuals prior to the commencement of site clearance works. Feasibility and suitability of transplanting the affected plant species of conservation interest would be carefully studied and suitable receptor sites would be identified during Tree Felling Application.	Whole Site / During Construction	Contractor	✓	✓				
S7.11	Avoid any damage and disturbance, particularly those caused by filling and illegal dumping, to the surrounding habitats through proper management of waste disposal.	Whole Site / During Construction	Contractor	✓	✓				
S7.11	Regularly check the Site boundaries to ensure that they are not breached and that no damage occurs to surrounding areas Whole Site / During	Whole Site / During Construction	Contractor	✓	✓				
S7.11	Prohibit and prevent open burning within the site boundary during construction and provide temporary fire fighting equipment in the work areas.	Whole Site / During Construction	Contractor	✓	✓				
S7.11	Reinstate temporary work sites/disturbed areas immediately after completion of the construction works	Whole Site / During Construction	Contractor	✓	✓				
S7.11	Provide additional stream/river habitat with natural bottom (~2.1 ha) after the advanced works	Whole Site / During Construction	Contractor	✓	✓				
S7.14	Adopt proper ecological design for the landscape works along the river banks, including the floodplain (the 1.9ha marshy low-lying grassland will be reinstated in the floodplains at Hong Kong side.	Along river bank and water retardation pond / During Design Stage	Designer(s)	✓					
S7.14	The implementation of landscape works (including compensatory planting) adopting ecological design at Hong Kong side shall be monitored.	Whole Site / During Construction	Designer(s)		✓				
S7.14	One-year bird monitoring programme shall be conducted to monitor the effectiveness of the re-provisioned/reinstated habitats	Operation	Project Proponent/ Contractor					✓	
5. Waste Management									
S9.6	<u>General</u> The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges	Contract mobilisation / During construction	Contractor	✓					Waste Disposal (Chemical Waste) (General) Regulation; Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes; WBTC No 5/99, Trip ticket System for Disposal of Construction and Demolition Material; Water Pollution Control Ordinance

S9.6	Nomination of approved personnel to be responsible for standard site practices, arrangements for collection and effective disposal to an appropriate facility of all wastes generated at the Project Site	Contract mobilisation / During construction	Contractor	✓		
S9.6	Training shall be provided to site personnel in proper waste management and chemical handling procedures, the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling.	Contract mobilisation / During construction	Contractor	✓		
S9.6	Provision of sufficient waste disposal points and regular collection for disposal.	Whole Site / During Construction	Contractor	✓		WBTC Nos. 6/2002 and 6/2002A, Enhanced Specification for Site Cleanliness and Tidiness. Works Bureau, Hong Kong SAR Government
S9.6	Appropriate measures to reduce windblown litter and dust transportation of waste by either covering trucks or by transporting wastes in enclosed containers	Whole Site / During Construction	Contractor	✓		
S9.6	Separation of chemical wastes for special handling and appropriate Treatment Chemical Waste Treatment Centre at Tsing Yi.	Whole Site / During Construction	Contractor	✓		Waste Disposal (Chemical Waste) (General) Regulation
S9.6	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors	Whole Site / During Construction	Contractor	✓		
S9.6	A recording system for the amount of wastes generated/recycled and disposal sites.	Whole Site / During Construction	Contractor	✓		
S9.6	<i>Waste Reduction Measures</i> i. Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal. ii. Encourage collection of aluminium cans and waste paper by individual collectors during construction with separate labelled bins provided to segregate these wastes from other general refuse by the workforce. iii. Any unused chemicals and those with remaining functional capacity will be recycled as far as possible	Whole Site / During Construction	Contractor	✓		WBTC Nos. 6/2002 and 6/2002A, Enhanced Specification for Site Cleanliness and Tidiness
S9.6	iv. Use of reusable non-timber formwork to reduce the amount of C&D materials	Whole Site / During Construction	Contractor	✓		Works Branch Technical Circular (WBTC) No.32/92, The Use of Tropical Hard Wood on Construction Site
S9.6	v. Prior to disposal of construction waste, wood, steel and other metals will be separated to the extent practical, for re-use and/or recycling to reduce the quantity of waste to be disposed of to landfill	Whole Site / During Construction	Contractor	✓		
S9.6	vi. Proper storage and site practices shall be adopted to reduce the potential for damage or contamination of construction materials	Whole Site / During Construction	Contractor	✓		
S9.6	vii. Plan and stock construction materials carefully to reduce amount of waste generated and avoid unnecessary generation of waste	Whole Site / During Construction	Contractor	✓		

S9.6	<p><i>Excavated Materials</i></p> <p>The contractor of the advanced work should open a billing account with EPD for the payment of disposal charges. A trip-ticket system will be established in accordance with ETWB TC(W) No. 31/2004 to monitor the reuse of surplus excavated materials off-site and disposal of construction waste and general refuse at landfills, and to control fly-tipping</p>	Contract mobilisation / During construction	Contractor	✓	✓	Waste Disposal (Charges for Disposal of Construction Waste) Regulation ETWB TC(W) No.31/2004
S9.6	<p>Ways to minimise generation of C&D materials include:</p> <p>(i) The Contractor is required to submit the Waste Management Plan (WMP) for approval by the Engineer with appropriate mitigation measures to deal with and allow space for waste segregation. Different C&D materials should be sorted into different categories for re-use/recycle. Day-to-day site operations of the Contractor should be closely monitored to ensure compliance with the approved WMP.</p> <p>(ii) The Designer shall ensure that the design of levels and dimensions are reasonably accurate to avoid unnecessary demolition, excavation and fill.</p> <p>(iii) The Contractor shall be encouraged to use long lasting materials such as steel and poly-fibre for formwork on site.</p> <p>(iv) The RSS shall control the disposal of public fill and C&D waste to the designated public filling facilities and landfills respectively through the implementation of a trip-ticket system according to ETWB TC(W) No. 31/2004.</p>	Whole Site / During Construction	Contractor	✓		
	<p>Ways to maximize the use of inert C&D material include:</p> <ol style="list-style-type: none"> The Contractor shall review the WMP quarterly to improve the site practice and maximise the use of inert C&D material Different sections of works shall be programmed to ensure the C&D materials generated could be re-used by the other sections of works or works contracts. Temporary storage areas should be identified to resolve programming mismatch between excavation and filling works. The excavated soft inert C&D materials should be reused for backfilling the boundary patrol road, channel embankment, etc. whenever practicable. Good quality top soil should be reused for landscaping. 	Whole Site / During Construction	Contractor	✓		
	<p>Ways to maximise the re-use/recycle of C&D material and/or rock on site include:</p> <ol style="list-style-type: none"> Recyclable materials such as wood and metal should be salvaged for reuse and inert materials utilized as public fill. Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of material and their proper disposal. Prior to disposal of C&D waste, it is recommended that wood, steel and other metals be separated for re-use and/or recycling and inert waste utilized as fill material to minimize the quantity of waste to be disposed of at landfills. 	Whole Site / During Construction	Contractor	✓		
S9.6	<p>Ways to maximise the use of recycled C&D materials include:</p> <ol style="list-style-type: none"> Relevant clauses would be incorporated in the Particular Specifications to facilitate the use of recycled aggregates as far as practicable, such as, temporary works, general fills and road sub-base. 	Whole Site / During Construction	Contractor	✓		
S9.6	<p>To reduce the potential dust impacts of the excavation works, the C&D materials will be wetted as quickly as possible to the extent practice after filling.</p>	Whole Site / During Construction	Contractor	✓		

S9.6	<p><i>Chemical Waste</i> Containers used for storage of chemical waste shall be:</p> <ol style="list-style-type: none"> Maintained in good condition and clearly labelled in both English and Chinese; Suitable for the substance they are holding, resistant to corrosion, and securely closed; and Capacity of less than 450 L unless the specifications have been approved by the EPD. 	All facilities / During construction	Contractor	✓		Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling, and Storage of Chemical Wastes
S9.6	<p>Storage areas for chemical waste shall:</p> <ol style="list-style-type: none"> Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have adequate ventilation; Be arranged so that incompatible materials are appropriately separated Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; and Be covered to prevent rainfall from entering 	All facilities / During construction	Contractor	✓		
S9.6	Any unused chemicals and those with remaining functional capacity shall be recycled to the extent practical.	Land Site / During Construction	Contractor	✓		
S9.6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi/ During construction	Contractor	✓		Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling, and Storage of Chemical Wastes
S9.6	<i>General Refuse</i> General refuse shall be timely cleared and shall be disposed of to the nearest licensed facility by reputable waste collector on regular basis to reduce odour, pest and litter impacts.	All areas / During construction	Contractor	✓		WBTC Nos. 6/2002 and 6/2002A, Enhanced Specification for Site Cleanliness and Tidiness.
S9.6	No waste shall be burnt on site. Wastes shall be collected by licensed waste haulier and be disposed of at licence sites.	Land Site / During Construction	Contractor	✓		Air Pollution Control Ordinance
S9.6	Training will be provided to workers on the concepts of site cleanliness and appropriate waste management procedures, including waste reduction, reuse and recycling at the beginning of the construction works.	All areas / During construction	Contractor	✓		
S9.8	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site inspection and audit programme shall be undertaken.	All facilities / During construction	ET and IEC	✓		
S9.8	Waste Management Plan (WMP) will be prepared and implemented in accordance with ETWB TC(W) No. 19/2005.	All facilities / During construction	Contractor	✓		ETWB TC(W) No.19/2005

6. Cultural Heritage							
			Whole Site / During Construction	Project Proponent			Antiquities and Monuments Ordinance
S11.8.1	Pursuant to the Antiquities and Monuments Ordinance, the project proponent should inform the AMO immediately in case of discovery of antiquities or supposed antiquities in the course of soil excavation works in construction stage.		Additional works boundary not covered in EIA / During design stage	Design Team and the Project Proponent (i.e. DSD)	✓		EIAO TM, Guidelines for CHIA, Antiquities and Monuments Ordinance
S11.8.1	In case the works boundary of the Project changes during the detailed design stage to cover additional area not being assessed, the need for further archaeological survey and subsequent impact assessment should be reviewed and AMO should be consulted.						
7. Landscape & Visual							
S12.6.10	MM1: Tree Protection and Preservation - Trees/ woodland within the Project Site will be protected and preserved as far as possible in accordance with ETWB TCW No. 29/2004 and 3/2006.		Land Site / During Construction	Contractor	✓		
S12.6.10	MM2: Tree Transplantation – Should removal of trees be unavoidable due to construction impacts, trees will be transplanted or felled according to the Detailed Tree Survey and Tree Felling Application. Established trees of value are to be re-located where practically feasible.		Land site / During Construction	Contractor(s)	✓		
S12.6.10	MM3: Minimize Disturbance – temporary structures and construction works should be planned with care to minimize disturbance to existing built structures as well as vegetation including riparian vegetation along the river.		Land Site / During Construction	Contractor	✓		
S12.6.10	MM4: Compensatory Tree Planting - Where loss of existing trees is unavoidable, compensatory planting of trees should be provided in accordance with ETWB TCW No. 03/2006 to compensate for those trees felled. Space is to be allowed within the Project Site (mainly planting in riverbank landscape areas of ~4.1 ha) for such planting. Plants will have 12 months to establish. Approximately 0.5 ha of compensatory woodland planting (in addition to the reinstatement of the woodland (LR4) if unavoidably affected) will be provided within the Project Site near Pak Fu Shan. The proposed compensatory woodland planting site will locate adjoining to the reinstated and existing (undisturbed by the Project) woodland on hillside. The selection of planting species shall be made with reference to the species identified in the Tree Survey and be native to Hong Kong or the South China region. The compensatory woodland planting should also adopt ecological design, ie provision of rare butterfly species larval food plant (Trema sp.), and further details refer to Section 7.1.3 of the EIA Report. The arrangement of the on-site compensatory planting, ie tree/ shrub mix and Trema sp., will be subject to detailed landscape design and planting plan, and recommended to be implemented prior to the construction activities as far as practical		Compensatory planting area / During Construction	Contractor	✓		
S12.6.10	MM5: Screening – Stockpiles of materials should be covered or hoarding erected where possible to reduce undesirable views of the construction site (such as stockpile areas), having consideration of safety and security. It is proposed that screening be compatible with the surrounding environment and where possible, non-reflective, recessive colours be used. Hoarding should be taken down at the end of the construction period.		Land Site / During Construction	Contractor	✓		

S12.6.10	MM6: Light Control – Control of night time lighting glare shall be implemented to minimize glare impact to adjacent VSRs.	Whole Site / During Construction	Contractor	✓			
S12.6.10	MM7: Reinstatement – Terrestrial areas temporarily disturbed by the Project during construction, should be re-vegetated with shrubs, ground cover or grass in order to restore the green ambience or LR as existed before the commencement of the Project to blend with the new environment, eg the earth embankment underneath the boundary patrol road near Pak Fu Shan should be planted to ensure the embankment structure blends in with the new environment.	Whole Site / During Construction	Contractor	✓			
S12.6.10	MM8: Buffer Planting – Tree and Shrub planting shall be provided for screening the natural watercourse, woodland and shrubby grassland on lowland, proposed boundary control road and fencing, where needed and taking into account security and boundary control limitations.	Appropriate location / During Construction	Contractor	✓			
S12.6.10	MM9: River Area Enhancement Landscaping – The river bed should be non-concreted as far as practical. The River bank and margins of approximately 4.1 ha should be enhanced with vegetation to compensate for the loss of existing vegetation and to enhance the visual and landscape value of the river where slope gradient allows. The typical design of riverbank landscaping areas for the Project is presented in Section 7.11.3 and Figure 7.11 of the EIA Report. The overall objectives for the landscaping works will be mainly concerned with ecological enhancement but also include landscape enhancement. For the sloping banks of the river, in order to guarantee safety of flood prevention, ecologically and environmentally friendly materials will be used as far as possible. The preliminary proposed landscape treatment along the sloping river banks can be classified into three types: natural vegetation, semi-natural and artificial. Further details of the river area enhancement plans can be found in Section 3 of the EIA Report, including protection of river bed with armour rock only where necessary and provision of grassed, cellular, reinforced concrete eco-friendly slope protection. Eco-bags are made of UV-resistant Polyethylene gas filled with fiber soil. Final details of the landscaping will be prepared during the detailed design stage of the Project.	Appropriate location / During Construction	Contractor	✓	✓		
S12.6.10	MM11: Floodplain Areas - The areas bound by sharp turns in the natural meander of the river should be made into floodplain areas to retain some of the riparian landscape at the river margins. The overall objectives for the landscaping works will be mainly concerned with ecological enhancement but also include landscape enhancement (also refer to Section 7.11.3 of the EIA Report). Further details will be developed during Detailed Design Stage.	Floodplain areas / During Construction	Contractor	✓	✓		
S12.6.10	MM12: Colours of Structures - Colours for the structures eg fences should be chosen to complement the surrounding area. Lighter colours such as shades of light grey, off-white and light brown may be utilised where technically feasible to reduce the visibility of the structures.	Whole Site / During Construction	Contractor	✓			
S12.6.10	MM13: Topsoil Reuse - Excavated topsoil should be conserved for re-use by the Project or other projects.	Whole Site / During Construction	Contractor	✓			
S12.9	The completed landscape works adopting ecological design on the Hong Kong side will be monitored during the one year establishment period.	Whole site / During 1 year Establishment period	Landscape Contractor	✓			

ANNEX D

THREE- MONTH ROLLING PROGRAM

ID	Task Name	Duration	Start	Finish	11.August	10.9	4.11	21.Novembre	102
568	17. Electrical meter cabinet of HKPF Lo Fong Bridge Post at CH R 0-980	1 day	22/7/2013	22/7/2013					
569	CH R 1-000 to 1-500	261 days	20/4/2013	5/3/2014					
570	1. Site clearance	45 days	20/4/2013	14/6/2013					
571	2. Setting out	7 days	24/4/2013	18/6/2013					
572	3. UU detection	7 days	26/4/2013	4/5/2013					
573	4. Drain pipe	42 days	11/5/2013	22/7/2013					
574	5. Primary Boundary Fence Foundation	95 days	29/6/2013	22/10/2013					
575	6. Secondary Boundary Fence Foundation	95 days	29/6/2013	22/10/2013					
576	7. Fill between Primary & Secondary Boundary Fence Foundation	51 days	4/9/2013	5/11/2013					
577	8. Lay cable ducting and drawpit for Security lighting	49 days	18/9/2013	16/11/2013					
578	9. Boundary Patrol Roadworks	97 days	6/11/2013	5/3/2014					
579	10. Utility reserved ducts under	18 days	30/4/2013	22/5/2013					
580	11. Fill outside PBF & SBF foundation	45 days	23/10/2013	19/12/2013					
581	12. Drainage works	56 days	14/12/2013	24/2/2014					
582	13. Primary Boundary Fence	33 days	2/10/2013	3/12/2013					
583	14. Secondary Boundary Fence	38 days	2/10/2013	15/11/2013					
584	CH R 1-500 to -2+050	359 days	15/6/2013	25/8/2014					
585	1. Site clearance	30 days	15/6/2013	20/7/2013					
586	2. Setting out	45 days	19/6/2013	10/8/2013					
587	3. UU detection	7 days	21/6/2013	28/6/2013					
588	4. Box Culvert	136 days	29/6/2013	9/12/2013					
589	5. Primary Boundary Fence Foundation	192 days	29/6/2013	19/2/2014					
590	6. Secondary Boundary Fence Foundation	144 days	29/6/2013	18/12/2013					
591	7. Fill between Primary & Secondary Boundary Fence Foundation	146 days	6/9/2013	5/3/2014					
592	8. Lay cable ducting and drawpit for Security lighting	144 days	21/9/2013	17/3/2014					
593	9. Boundary Patrol Roadworks	93 days	8/3/2014	28/6/2014					
594	10. Utility reserved ducts under BC2	14 days	29/6/2013	16/7/2013					
595	11. Fill outside PBF & SBF foundation	45 days	20/2/2014	14/4/2014					
596	12. Drainage works	110 days	15/4/2014	25/8/2014					
597	13. Primary Boundary Fence	58 days	11/7/2014	23/3/2014					
598	14. Secondary Boundary Fence	72 days	11/7/2014	21/9/2014					
599	Landscaping	24 days	26/2/2014	20/1/2015					
600	Security system by ENSD	185 days	12/8/2013	25/9/2014					
601	Construction of Portion B CH R 2-050 to CH R 2-838	445 days	29/6/2012	24/12/2013					
602	Possession of Site	1 day	29/6/2012	29/6/2012					
603	Notification to EPD (EP 430)	77 days	21/5/2012	20/8/2012					
604	11KV cable CH R 2+130 to 2+838	30 days	23/9/2013	29/10/2013					
605	Temporary diversion of 11KV cable in Portion B by CLP	60 days	26/9/2012	7/12/2012					
606	Pillar box for security lighting	21 days	16/8/2013	9/9/2013					
607	LV Switchroom for security lighting PL02 at CH R 2-225	21 days	16/8/2013	9/9/2013					
608	Security Lighting pole SL083 - 114	196 days	21/11/2012	23/7/2013					
609	E & M	14 days	31/11/2013	19/2/2013					
610	Pedestrian Gate	147 days	16/12/2013	18/7/2013					
611	Geotechnical Instrumentation	16 days	19/9/2013	9/10/2013					
612	Traffic sign & frontier closed area warning sign	15 days	19/9/2013	8/10/2013					
613	Road marking	3 days	19/9/2013	23/9/2013					
614	CH R 2-050 to 2-500	445 days	29/6/2012	24/12/2013					
615	1. Site clearance	30 days	29/6/2012	3/8/2012					
616	2. Setting out	45 days	4/8/2012	25/9/2012					
617	3. UU detection	7 days	13/8/2012	20/8/2012					
618	4. Box Culvert No.4 at CH R 2+764	43 days	21/8/2012	11/10/2012					
619	5. Drain pipe (N/S)	0 days	38/2/012	3/8/2012					
620	6. Primary Boundary Fence Foundation	401 days	21/8/2012	24/12/2013					
621	CH R 2-500 to 2-838	367 days	29/6/2012	21/9/2013					
622	1. Site clearance	30 days	29/6/2012	3/8/2012					
623	2. Setting out	45 days	4/8/2012	25/9/2012					
624	3A. UU detection	7 days	10/8/2012	17/8/2012					
625	3B. Drain Pipe	60 days	21/8/2012	1/11/2012					
626	4. Primary Boundary Fence Foundation	244 days	18/8/2012	17/6/2013					
627	5. Secondary Boundary Fence Foundation	186 days	29/10/2012	17/6/2013					
628	6. Fill between Primary & Secondary Boundary Fence Foundation	198 days	29/10/2012	2/7/2013					
629	7. Lay cable ducting and drawpit for Security lighting	196 days	12/11/2012	13/7/2013					
630	8. Boundary Patrol Roadworks	239 days	30/11/2012	21/9/2013					
631	9. Temporary Road	49 days	1/2/2013	6/4/2013					
632	10. Fill outside PBF & SBF foundation	30 days	18/6/2013	23/7/2013					
633	11. Drainage works	24 days	24/7/2013	20/8/2013					
634	12. Primary Boundary Fence	194 days	12/11/2012	11/7/2013					
635	13. Secondary Boundary Fence	7 days	3/7/2013	10/7/2013					
636	14. Landscaping	105 days	26/9/2012	1/2/2013					
637	Security system by ENSD	121 days	8/2/2013	11/7/2013					
638	1. Installation	120 days	8/2/2013	10/7/2013					
639	2. Testing and Commissioning	1 day	11/7/2013	11/7/2013					

Project No: DC201108
Date: 2/10/2012

Task Split

Project Summary

External Milestone

Include Task

Exclude Milestone

Manual Task

Manual Summary

Manual Summary Ratio

Bar-only

Manual Summary

Bar-only

Finish-only

Critical

Critical Split

Progress

Deadline

ID	Task Name	Duration	Start	Finish
1921	Construction of Portion C CH_R 2+838 to CH_R 4+271	619 days	27/12/2012	24/12/2015
1922	Possession of Site	1 day	27/12/2012	27/12/2012
1923	TKS cable CH_R 2+838 to 4+271	138 days	14/9/2013	4/3/2014
1926	Pillar box for security lighting	30 days	28/2/2013	5/9/2013
1931	LV Switchroom for security lighting PL03 at CH_R 4+090	21 days	8/3/2014	1/4/2014
1933	Security Lighting pole SL115 - 170	96 days	14/5/2013	5/9/2013
1941	E & M	21 days	9/7/2013	1/8/2013
1945	Gate	69 days	14/5/2013	5/8/2013
1946	1. Pedestrian Gate	43 days	15/6/2013	5/8/2013
1949	2. Vehicle Pedestrian Gate	36 days	14/5/2013	26/6/2013
1952	3. Vehicular Gate	10 days	21/6/2013	3/7/2013
1955	Geotechnical Instrumentation	256 days	30/4/2013	8/3/2014
1970				
1971				
1972				
1973				
1974				
1975				
1976				
1977				
1978				
1979				
1980				
1981				
1982				
1983				
1984				
1985				
1986				
1987				
1988				
1989				
1990				
1991				
1992				
1993				
1994				
1995				
1996				
1997				
1998				
1999				
2000				
2001				
2002				
2003				
2004				
2005				
2006				
2007				
2008				
2009				
2010				
2011				
2012				
2013				
2014				
2015				
2016				
2017				
2018				
2019				
2020				
2021				
2022				
2023				
2024				
2025				
2026				
2027				
2028				
2029				
2030				
2031				
2032				
2033				
2034				
2035				
2036				
2037				
2038				
2039				
2040				
2041				
2042				
2043				
2044				
2045				
2046				
2047				
2048				
2049				
2050				
2051				
2052				
2053				
2054				
2055				
2056				
2057				
2058				
2059				
2060				
2061				
2062				
2063				
2064				
2065				
2066				
2067				
2068				
2069				
2070				
2071				
2072				
2073				
2074				
2075				
2076				
2077				
2078				
2079				
2080				
2081				
2082				
2083				
2084				
2085				
2086				
2087				
2088				
2089				
2090				
2091				
2092				
2093				
2094				
2095				
2096				
2097				
2098				
2099				
2100				
2101				
2102				
2103				
2104				
2105				
2106				
2107				
2108				
2109				
2110				
2111				
2112				
2113				
2114				
2115				
2116				
2117				
2118				
2119				
2120				
2121				
2122				
2123				
2124				
2125				
2126				
2127				
2128				
2129				
2130				
2131				
2132				
2133				
2134				
2135				
2136				
2137				
2138				
2139				
2140				
2141				
2142				
2143				
2144				
2145				
2146				
2147				
2148				
2149				
2150				
2151				
2152				
2153				
2154				
2155				
2156				
2157				
2158				
2159				
2160				
2161				
2162				
2163				
2164				
2165				
2166				
2167				
2168				
2169				
2170				
2171				
2172				
2173				
2174				
2175				
2176				
2177				
2178				
2179				
2180				
2181				
2182				
2183				
2184				
2185				
2186				
2187				
2188				
2189				
2190				
2191				
2192				
2193				
2194				
2195				
2196				
2197				
2198				
2199				
2200				
2201				
2202				
2203				
2204				
2205				
2206				
2207				
2208				
2209				
2210				
2211				
2212				
2213				
2214				
2215				
2216				
2217				
2218				
2219				
2220				
2221				
2222				
2223				
2224				
2225				
2226				
2227				
2228				
2229				
2230				
2231				
2232				
2233				
2234				
2235				
2236				
2237				
2238				
2239				
2240				
2241				
2242				
2243				
2244				
2245				
2246				
2247				
2248				
2249				
2250				
2251				
2252				
2253				
2254				
2255				
2256				
2257				
2258				
2259				
2260				
2261				
2262				
2263				
2264				
2265				
2266				
2267				
2268				
2269				
2270				
2271				
2272				
2273				
2274				
2275				
2276				
2277				
2278				
2279				

ANNEX E

MONTHLY SUMMARY WASTE FLOW TABLE

AND

**SUMMARY TABLE FOR WORK PROCESSES
OR ACTIVITIES REQUIRING TIMBER FOR TEMPORARY WORKS**

Monthly Summary Waste Flow Table

Name of Department: DSD

Contract No.: DC/2011/06

Monthly Summary Waste Flow Table for Nov 2012

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of Non C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m ³)
Jan-12	N/A	---	---	---	---	---	---	---	---	---	---
Feb-12	N/A	---	---	---	---	---	---	---	---	---	---
Mar-12	N/A	---	---	---	---	---	---	---	---	---	---
Apr-12	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
May-12	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.013
Jun-12	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.001
Jul-12	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Aug-12	0.007	0.000	0.007	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sep-12	0.002	0.000	0.002	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.154
Oct-12	0.003	0.000	0.003	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.058
Nov-12	0.005	0.000	0.005	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.042
Total	0.017	0.000	0.017	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.268

Notes :

- (1) Note Used.
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Sites.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- (4) The summary table shall be submitted to the Engineer's Representative monthly together with the Waste Flow Table for review and monitoring.

Summary Table for Work Processes or Activities Requiring Timber for Temporary Works

Contract No.: DC/2011/06

Contract Title: *Reprovisioning of Boundary Patrol Road and Associated Security Facilities between Ping Yuen River and Pak Fu Shan and Drainage Works in North District*

Report Period: Nov-12

Item No	Description of Works Process or Activity [see note (a) below]	Justifications for Using Timber in Temporary Construction Works	Est. Quantities of Timber Used (m ³)	Actual Quantities used (m ³)	Remarks
1	Transition formwork & falsework (Portion A,B,E)	Temporary formwork & falsework design	10	9	
2	Transition formwork & falsework (Portion A,B,C)	Temporary formwork & falsework design	25	18	
3	Transition formwork & falsework (Portion A,B,C,E)	Temporary formwork & falsework design	52	40	
4	Transition formwork & falsework (Portion A,B,C,E)	Temporary formwork & falsework design	77	72	
Total Estimated Quantity of Timber Used			164		

Notes

- (a) The Contractor shall list out all the work items requiring timber for use in temporary construction works. Several minor work items may be grouped into one for ease of updating.
- (b) The summary table shall be submitted to the Engineer's Representative monthly together with the Waste Flow Table for review and monitoring
