

Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, Shatin, N.T., Hong Kong Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Our Ref. : TEEM/334/18/L/060 Date : 13 June 2018

By Hand

Environmental Protection Department

Environmental Assessment Division Metro Assessment Group, Kowloon Section (2) 27/F Southorn Centre, 130 Hennessy Road Wan Chai, Hong Kong

Attn: Ms. Kwok Wing Chi, Winnie

Dear Madam,

Contract No. SS D505 Environmental Permit No. EP-454/2013 Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-Vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area <u>Submission of Environmental Impact Monitoring Report May 2018</u>

We are writing, on behalf of Environmental Permit Holder, Food and Environmental Hygiene Department, to provide four hard copies and one electronic copy of Environmental Impact Monitoring Report May 2018 for your record in accordance with Condition 3.4 of EP-454/2013.

Should you have any questions, please do not hesitate to contact the undersigned at (852) 3610 8777 or our Ir. Nelson Tam at (852) 3610 8701. Thank you.

Yours faithfully,

For and on behalf of **Telemax Environmental and Energy Management Limited**

Ir Eagle MO Managing Director

EM / NT)/SC / KM / WW

Encl.

c.c. ArchSD – Mr. Sing-hin SAT, Saadullah / Mr. WAN Koon Piu, Dick (by hand) FEHD – Ms. May NG (by hand)
PTA – Ms. Clara PANG / Mr. Jess YEUNG (by email)
AEC – Ms. Grace KWOK / Mr. HO Tin Kit (by email)
CRBC – Mr. Vincent CHUNG / Mr. FU Kwok Kwan (by email)



Allied Environmental Consultants Limited

Acousticians & Environmental Engineers

19/F., Kwan Chart Tower, 6 Tonnochy Road, Wan Chai, Hong Kong Tel.: (852) 2815 7028 Fax: (852) 2815 5399 Email: info@aechk.com

Our Ref: 1330/18-0014

13 June 2018

Food and Environmental Hygiene Department Planning & Development Section Room 101, 1/F, New Wan Chai Market 258 Queen's Road East, Wan Chai, Hong Kong

Attn: Ms. Lorraine Lo

Dear Madam,


Contract No. SS D505 Environmental Permit No. EP-454/2013 Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-Vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area Independent Environmental Checker for Construction Phase Condition 3.4 – Submission of Monthly EM&A Report for May 2018 (Issue 3)

Further to the receipt from Environmental Team (ET) of the captioned Monthly EM&A Report on 11th and 12th June 2018 via email, pursuant to Condition 3.4 of Environmental Permit, I hereby verify the captioned report (Issue 3).

Yours faithfully, For ALLIED ENVIRONMENTAL CONSULTANTS LIMITED

Grace Kwok Independent Environmental Checker GK/cwh

C.C.			
FEHD		Ms. May NG, ASO(P)4/ Mr. Vincent TAM, CTSO(Ops)2	Email
ArchSD		Mr. Shing-hin SAT, Saadullah, SPM335 / Mr. WAN Koon Piu, Dick, PM342	Email
PTA		Ms. Clara PANG / Mr. Jess YEUNG	Email
TEEM	(ET Leader)	Mr. Jason LAU	Email
CRBC	(Main Contractor)	Mr. Vincent CHEUNG, Project Manager / Mr. KK FU, Site Agent	Email



By Email

Recycled Pape



FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot, Yen Ming Road, West Kowloon Reclamation Area

Environmental Monitoring and Audit Report

Prepared by: Telemax Environmental and Energy Management Limited

Prepared by:

TELEMAX

13 June 2018 Date

Certified by: Ir. Nelson Tam

ENVIRONMENTAL TEAM LEADER

13 June 2018

Date

Verified by: Ms. Grace Kwok

INDEPENDENT ENVIRONMENTAL CHECKER

13 June 2018

Date



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Issue	Date	Prepared by	Checked by	Approved by	Remark
1	7 th June 2018	Kiwi Man (Assistant Consultant)	Nelson Tam (Associate) / Susan Chen (Senior Consultant) Eagle Mo (Managing Director)		
2	12 th June 2018	Kiwi Man (Assistant Consultant)	Nelson Tam (Associate) / Susan Chen (Senior Consultant)Eagle Mo (Managing Director)		Incorporating AEC's comment
3	12 th June 2018	Kiwi Man (Assistant Consultant)	Nelson Tam (Associate) / Susan Chen (Sentior Consultant)	Eagle Mo (Managing Director)	Incorporating AEC's comment





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

LIST OF CONTENTS

1.0	Executive Summary
2.0	Project Information
3.0	Environmental Status
4.0	Summary of EM&A Requirement7
5.0	Implementation Status of Environmental Mitigation Measures 11
6.0	Monitoring Methodology13
7.0	Monitoring Results
8.0	Non-compliance, Complaints, Notifications of Summons and Status of Prosecutions 18
9.0	Forecast of Works Programme and Future Key Issues
10.0	Solid and Liquid Waste Management Status
11.0	Comments, Recommendations and Conclusions





List of Table

Table 1	Contact Details of Key Personnel			
Table 2	Status of Licenses and Permits			
Table 3	Summary of the Submission under the EP			
Table 4	Interrelationship between Construction Activities and Mitigation			
	Measures			
Table 5	Action and Limit Levels for Construction Noising Monitoring			
Table 6	Event and Action Plan for Construction Noise Monitoring			
Table 7	Summary of Site Inspections			
Table 8	Noise Monitoring Equipment			
Table 9	Representative Noise Sensitive Receivers Identified for			
	Construction			
Table 10	Noise Monitoring Results at NSR1			
Table 11	Noise Monitoring Results at NSR7			

Appendix

Appendix A	Master Programme
Appendix B	Organization Chart
Appendix C	Inspection Checklist
Appendix D	Calibration Certificates
Appendix E	Impact Monitoring Data of Noise
Appendix F	Graphical Plot of Leq
Appendix G	Monitoring Schedule
Appendix H	Project Layout
Appendix I	Location of the Impact Monitoring Locations
Appendix J	Photo Records of Monitoring
Appendix K	Cumulative Statistics on Complaints, Notifications of Summons
	and Successful Prosecutions
Appendix L	Monthly Waste Flow Table
Appendix M	Environmental Licenses / Permits
Appendix N	NSR 1 School Calendar 2017-18





1.0 Executive Summary

1.1 In December 2015, Telemax Environmental and Energy Management Limited (TEEM) was appointed to conduct an Environmental Monitoring and Audit (EM&A) program for the proposed reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot, Yen Ming Road, West Kowloon Reclamation Area (FEHD). The site clearance and tree felling works were undertaken during the period from 10th December 2015 to 7th February 2016. The construction works were commenced on 29th February 2016 and all EM&A works were undertaken in accordance with the EM&A Manual and the requirements under the Environmental Permit EP-454/2013. This report is the twenty-sixth monthly EM&A report, which detailed the environmental monitoring and audit results recorded during the period from 1st May 2018 to 31st May 2018.

Reporting Change

1.2 There was no reporting change required in the reporting month.

Record of Complaints

1.3 No environmental complaint was recorded in the reporting month.

Record of Notification of Summons and Successful Prosecution

1.4 No notification of summons and successful prosecution was received in the reporting month.





- 1.5 Key issues to be considered in the coming three months included:
 - Properly store and label oils and chemicals on site;
 - Chemical, chemical waste and waste management;
 - Sorting, recycling, storage and disposal of general refuse and construction waste;
 - Properly maintain all drainage facilities and wheel washing facilities on site;
 - Generation of dust from construction works;
 - Noise impact from operation equipment and machinery on site;
 - Generation of site surface runoffs and wastewater from activities on site; and
 - Tree protective measures for all retained trees should be well maintained.





2.0 Project Information

Background

- 2.1 The project proponent is the reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot, Yen Ming Road, West Kowloon Reclamation Area (FEHD) and the Works Agent is the Architectural Services Department (ArchSD).
- 2.2 The proposed office-cum-vehicle depot building will be a five-story building comprising various facilities for vehicle washing and repair operation, parking of vehicles as well as offices. It will occupy a site area of about 8,278 m².
- 2.3 The FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot is categorized as a designated project under the Environmental Impact Assessment Ordinance (EIAO) and therefore a detailed Environmental Impact Assessment (EIA-216/2013) has been conducted in year 2013 and an Environmental Permit number EP-454/2013 was issued by Environmental Protection Department in November 2013.
- 2.4 The subject site is located at Yen Ming Road, West Kowloon Reclamation Area given in *Appendix H*. The subject site is bounded to the north by Nam Cheong Station, to the east by CLP Tak Kok Tsui Substation, to the south by Yuen Fat Building, and to the west by Cheung Sha Wan Wholesales Fish and Food Markets. Sir Ellis Kadoorie Secondary School (West Kowloon) and Fu Cheong Estate Fu Yun House, being the nearest educational and residential establishment, are located at around 100m and 270m from the site boundary respectively.
- 2.5 Key personnel and contact particulars are summarized in *Table 1*.

Role	Department / Company	Names	Contact Number
Project Proponent	Food and Environmental Hygiene Department	Ms. Lorraine Lo	3141 1227
Works Agent	Architectural Services Department	Mr. Sing-hin Sat	2867 3843
Architect's representative	P&T Architects and Engineers (Architectural)	Mr. Jess Yeung	2832 7410
Main Contractor	China Road and Bridge Corporation	Mr. Vincent Chung	2283 1688
Environmental Team Leader	Telemax Environmental and Energy Management Ltd.	Ir. Nelson Tam	3610 8701
Independent Environmental Checker	Allied Environmental Consultants Ltd.	Ms. Grace Kwok	2815 7028

Table 1 Contact Details of Key Personnel







- 2.6 The construction programme is referred to **Appendix A** and the management structure is given in **Appendix B**.
- 2.7 The major works undertaken and/or completed during the reporting month are listed as below:
 - General housekeeping;
 - Plastering works;
 - Spatterdash works;
 - Installation of block wall;
 - Erection of bamboo scaffold, block wall and block wall metal frame;
 - Backfilling works;
 - Planting works;
 - Dismantling of formworks and falsework;
 - Liquid applied waterproofing membrane; and
 - Screeding works.





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Environmental Status 3.0

Status of the Statutory Environmental Compliance

3.1 The EM&A Works follow the EP conditions under the Environmental Impact Assessment Ordinance (EIAO) and a summary of the submission under the EP for this project up to the reporting month is presented in *Table 2 & Table 3* below:

			Valid Period		License/	
Statutory	License/	License or			Permit	Remarks
Reference	Permit	Permit No.	From	То	Holder	Kelliai KS
	Environmental					
EIAO	Permit	EP-454/2013	12-Nov-13	N/A	FEHD	-
WPCO	Discharge License (Site)	WT00023331-2015	22-Jan-16	31-Jan-21	CRBC	Discharge of Industrial Trade Effluent in Contract No. SS D505 was approved on 22 Jan 2016.
WDO	Chemical Waste Producer Registration	5213-269-C1232-18	15-Jan-16	N/A	CRBC	Chemical waste produced in Contract No. SS D505. The application was approved on 15 Jan 2016.
WDO	Billing Account for Disposal of Construction Waste	7024032	21-Dec-15	N/A	CRBC	Waste disposal in Contract No. SS D505. The application was approved on 21 Dec 2015.
NCO	Construction Noise Permit	GW-RE0978-17	3-Jan-18	30-Jun-18	CRBC	Use of prescribed powered mechanical equipment during nighttime. (0000 to 2400 hours on general holidays, including Sundays, 0000 to 0700 hours and 1900-2400 hours on any day not being a general holiday.). The permit was approved on 18 December 2017.

Table 2 Status of Licenses and Permits

The copies of environmental licenses or permits are enclosed in Appendix M.





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com Table 3 Summary of the Submission under the EP

EP-454/2013 Clause No.	Submission Status
1.12	Notification of commencement date of construction on 15th January 2016
2.4	Landscape and Visual Mitigation Plan submitted on 27th January 2016
3.3	Baseline monitoring report submitted on 15th February 2016
3.4	Environmental Monitoring Report of April 2018 submitted on 14th May 2018
4.2 & 4.3	Dedicated web site set up on 11th April 2016

Mitigation Measures for Construction Works

3.2 According to the basic project information, the major construction works undertaken during the reporting month are listed in *Table 4*, showing the interrelationship between construction activities and environmental mitigation measures for the reporting month. In order to indicate the project site, an illustrative drawing is provided in *Appendix I* to demonstrate the location of works, the project area, environmental sensitive receivers and locations of the monitoring and control stations.





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Table 4 Interrelationship between Construction Activities and Mitigation Measures

Construction Works		Major Environmental Impact	Mitigation Measures
1. 2. 3. 4. 5. 6. 7. 8. 9.	General house keeping Plastering works; Spatterdash works; Installation of block wall; Erection of bamboo scaffold, block wall and block wall metal frame; Backfilling works; Planting works; Dismantling of formworks and falsework Liquid applied waterproofing membrane Screeding works	Construction dust, construction noise and waste management	 Tarpaulin cover was provided to minimize potential for damage or contamination of construction materials; Watering and impervious sheeting was provided to dusty materials; Water spraying should be provide to haul road and excavation works; Well-maintained and quiet plants were used; Proper waste storage and sorting was applied; Trip record was maintained properly; and Noise barrier was implemented during construction activities; Cement sealing, cover walkway pavement and pump addition were implemented.

4.0 Summary of EM&A Requirement

4.1 According to the environmental findings detailed in the Environmental Impact Assessment (EIA) report and the EM&A Manual of the Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area Project ("the Project"), the EM&A requirements of the noise, air quality, water quality, waste management, landscape and visual and environmental audit are summarized as follows:

Noise

4.2 The construction noise level should be measured in terms of the A-weighted equivalent continuous sound pressure level (L_{eq}). The $L_{eq(30min)}$ should be used as the monitoring parameter for the time period from 0700 to 1900 hours on normal weekdays. The supplementary information for data auditing and statistical results, such as L_{10} and L_{90} , should be should be obtained and recorded for reference.

Environmental Audit

4.3 Site inspections should be conducted regularly to ensure that appropriate environmental protection and pollution control mitigation measures for noise, air quality, water quality, waste management and landscape and visual aspects are properly implemented for the construction works activities associated with the Project, as they are one of the most





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com effective tools to enforce the environmental protection require

effective tools to enforce the environmental protection requirements at the works sites and works areas.

- 4.4 Regular site inspections should be carried out and led by the Architect's Representative and attended by the Contractor and ET at least once every week. The areas of inspection should not be limited to the environmental conditions, pollution control and mitigation measures within the works sites and works areas. It should also review the environmental conditions of that location that are beyond the boundary of the works sites and works areas likely to be affected directly or indirectly by the construction site activities. The ET Leader should make reference to the following information when conducting site inspection:
 - The EIA and EM&A recommendations on the environmental protection and pollution control mitigation measures;
 - On-going results of the EM&A programme;
 - The works progress and programme;
 - Proposals of individual works methodologies (which should include the proposal of the associated pollution control measures);
 - Contract specifications on environmental protection and pollution prevention control;
 - The relevant environmental protection and pollution control legislation; and
 - Previous site inspection findings that were undertaken by the ET and/or others.
- 4.5 The Contractor should keep the Architect's Representative and ET updated with all the relevant environmental related information on the construction contract to carry out the site inspections. The inspection findings and associated recommendations for improvements to the environmental protection and pollution control and outcome of the improvement should be recorded and followed up by the Contractor in an agreed timeframe.
- 4.6 The Architect's Representative, ET and Contractor should also carry out ad hoc site inspections if significant environmental problems are identified. Inspections may also be required subsequent to the receipt of environmental complaints, or as part of the investigation work, as specified in the Event and Action Plans for the EM&A





Action and Limit Level

4.7 Accordingly to the EM&A requirement only noise impact of the construction stage requires impact monitoring. Corresponding action and limit level is set up to provide an appropriate framework for the interpretation of monitoring results. The noise impact monitoring data shall be checked against the Action and Limit Levels as listed in *Table 5*.

Time Period	Action Level	Limit Level, Leq 30mins, dB(A)
0700-1900 hours on	When one documented complaint is	70 dB(A) for school
normal weekdays	received	65 dB(A) during examination period.
		75 dB(A) for residential premises

Table 5 Action and Limit Levels for Construction Noise Monitoring

Event and Action Plans

4.8 In case of non-compliance with the construction noise criteria, the contractor shall undertake corresponding actions in accordance with the Event and Action Plan given in EM&A Manual and shown in *Table 6*.



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Table 6 Event and Action Plan for Construction Noise Monitoring

Event	Action			
	ET	IEC	Architect's Representative	Contractor
Action	1. Notify the IEC and Contractor.	1. Review the analysed results	1. Confirm receipt of notification of failure	1. Submit noise mitigation proposals
Level	2. Carry out investigation.	submitted by the ET.	in writing.	to the IEC.
	3. Report the results of investigation to the IEC and	2. Review the proposed remedial	2. Notify the Contractor.	2. Implement noise mitigation
	Contractor.	measures by the Contractor and	3. Require the Contractor to propose	proposals.
	4. Discuss with the Contractor and formulate remedial	advise the Architect's	remedial measures for the analysed noise	
	measures.	Representative accordingly.	problem.	
	5. Increase monitoring frequency to check mitigation	3. Supervise the implementation of	4. Ensure remedial measures are properly	
	effectiveness.	remedial measures.	implemented.	
Limit	1. Notify the IEC, Architect's	1. Discuss amongst the Architect's	1. Confirm receipt of notification of failure	1. Take immediate action to avoid
Level	Representative, EPD and Contractor.	Representative, ET and	in writing.	further exceedance.
	2. Identify sources.	Contractor on the potential remedial	2. Notify the Contractor.	2. Submit proposals for remedial
	3. Repeat measurements to confirm findings.	action.	3. Require the Contractor to propose	action to the IEC within 3 working
	4. Increase monitoring frequency.	2. Review the Contractor's	remedial measures for the analysed noise	days of notification.
	5. Carry out analysis of the Contractor's working	remedial action whenever necessary	problem.	3. Implement the agreed proposals.
	procedures to determine possible mitigation to be	to assure their effectiveness and	4. Ensure remedial measures are properly	4. Resubmit proposals if problems
	implemented.	advise the Architect's	implemented.	still not under control.
	6. Inform the IEC, Architect's Representative and EPD the	Representative accordingly.	5. If exceedance continues, consider what	5. Stop the relevant portion of works
	causes and action taken for the exceedances.	3. Supervise the implementation of	portion of work is responsible and instruct	as determined by the Architect's
	7. Assess the effectiveness of the Contractor's remedial	remedial measures.	the Contractor to stop that portion of works	Representative until the exceedance
	action and keep the IEC, EPD and Architect's		until the exceedance is abated.	is abated.
	Representative informed of the results.			
	8. If exceedance stops, crease additional monitoring			

Note (1): ET – Environmental Team, IEC – Independent Environmental Checker; (2) Each step of action should be undertaken within 1 working day unless otherwise specified.





5.0 Implementation Status of Environmental Mitigation

Measures

- 5.1 During reporting month, major works undertaken and/or completed during the reporting month are listed as below:
 - General house keeping;
 - Plastering works;
 - Spatterdash works;
 - Installation of block wall;
 - Erection of bamboo scaffold, block wall and block wall metal frame;
 - Backfilling works;
 - Planting works;
 - Dismantling of formworks and falsework;
 - Liquid applied waterproofing membrane; and
 - Screeding works.
- 5.2 The relevant parties have implemented mitigation measures which include, but not limited to the following:
 - Tarpaulin cover was provided to minimize potential for damage or contamination of construction materials;
 - Watering and impervious sheeting was provided to dusty materials;
 - Water spraying was provided to haul road and excavation works;
 - Well-maintained and quiet plants were used;
 - Proper waste storage and sorting was applied;
 - Trip record was maintained properly;
 - Noise barrier was implemented during construction activities; and





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

- Cement sealing, cover walkway pavement and pump addition were implemented.
- 5.3 A total of 5 site inspections were conducted by the Environmental Team (ET) in this reporting period. Major observation by the ET, actions by the Contractor and outcome are summarized in *Table 7*.

Date	Non-compliances /	Action taken by	Outcome
	Observations / Reminders	Contractor	
3 rd May 2018	Nil.	Nil.	Nil.
9 th May 2018	Nil.	Nil.	Nil.
17 th May 2018	Nil.	Nil.	Nil.
23 rd May 2018	Nil.	Nil.	Nil.
30 th May 2018	Nil.	Nil.	Nil.

Table 7 Summary of Site Inspections

5.4 During site inspection in the reporting month, reminder and suggestion are made to the Contractor and corresponding environmental mitigation measures were observed. The implementation of environmental mitigation measures for construction stages stated in approved EIA Report, EM&A Manual and Environmental Permit were carried out properly as shown in Appendix C.





6.0 Monitoring Methodology

Monitoring Parameter

- 6.1 Impact noise monitoring was conducted at the designated noise monitoring location between 0700-1900 hours using a sound level meter which complies with the International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1).
- 6.2 Monitoring of $L_{eq(30min)}$ were carried out at each station at 0700-1900 hours on normal weekdays at a frequency of once a week when construction are underway. The L_{eq} , L_{10} and L_{90} were recorded at the specified intervals. The meter was mounted on a tripod at a height of 1.2m above ground with the microphone positioned at G/F adjacent the NSRs facing the works area.
- 6.3 Noise measurements were not be made in the presence of fog, rain, and wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s. The wind speed was checked with a portable anemometer capable of measuring the wind speed in m/s. Noise measurements were made when construction activities were underway.

Calibration and Maintenance

- 6.4 The calibration of the sound level meter and their respective calibrators were carried out according to the manufacturer's requirements. The sound level meter and the calibrator were calibrated at an accredited laboratory to ensure their performance and accuracy meet manufacturer's specifications.
- 6.5 Maintenance and calibration procedures are as follows:
 - The microphone head of the sound level meter and calibrator should be cleaned with a soft cloth at quarterly intervals; and
 - The sound level meter and calibrator should be calibrated annually





- 6.6 Immediately prior to and following each noise measurement the accuracy of the sound level meter was checked using the acoustic calibrator. Measurements shall be valid only if the calibration level, before and after the noise measurement, agree to within 1.0 dB.
- 6.7 The equipment shall be stored properly and well-maintained with regard to the manufacturer's recommendations. Noise instrumentation details are given in *Table 8* and the Calibration Certificates for the sound level meter and calibrator are given in *Appendix D*.

Item	Equipment	Model Number	Serial Number
1	Integrating Sound Level Meter	AWA5661	304042
2	Integrating Sound Level Meter	AWA5661	301143
3	Calibrator	ND9	507258

Table 8 Noise Monitoring Equipment

Monitoring Locations

6.8 The designated locations for the construction noise monitoring are listed in *Table 9* and shown in *Appendix I*.

NSR ID	Location	NSR Type
NSR1	Sir Ellis Kadoorie Secondary School (West Kowloon)	Educational Premises
NSR7	Fu Cheong Estate Fu Yun House	Residential Premises

Table 9 Representative Noise Sensitive Receivers Identified for Construction

NSR denotes Noise Sensitive Receivers





7.0 Monitoring Results

- 7.1 Impact noise monitoring was conducted at Sir Ellis Kadoorie Secondary School (NSR1) and Fu Cheong Estate Fu Yun House (NSR7) on 3rd, 9th, 15th, 21st and 26th May 2018.
- 7.2 Noise monitoring results in terms of $L_{eq(30min)}$, $L_{10(30min)}$ and $L_{90(30min)}$ measured at Sir Ellis Kadoorie Secondary School (NSR1) and Fu Cheong Estate Fu Yun House (NSR7) are summarized in *Table 10* and *Table 11* respectively and the corresponding graphical plot and field record sheet are given in **Appendix E**. The field record sheets recorded the measured noise levels according to façade measurements. L_{10} and L_{90} represent sound levels that are exceeded 10% and 90% of the time respectively. Normally, L_{10} measurements can be considered as the average peak levels, whilst L_{90} levels can be considered as the average background noise levels. No exceedance was found during the reporting period at both NSR1 &NSR7 according to the monitoring results.





NSR1		Sir	Ellis Kadoo	rie Second	lary School		
Date	Monitoring Time Period	Weather Condition	Wind Speed (m/s)	L10(30 min)	L90(30 min)	Leq(30 min)	Limit Level
3/5/2018	5/2018 07:00-19:00		<5	66.3	59.9	64.2	70.0
9/5/2018	07:00-19:00	Cloudy	<5	66.5	60.7	64.4	70.0
15/5/2018	5/5/2018 07:00-19:00		<5	66.5	60.2	64.4	70.0
21/5/2018	07:00-19:00	Fine	<5	66.4	60.0	64.3	70.0
26/5/2018	07:00-19:00	Sunny	<5	66.4	60.7	64.3	70.0
	Average L	eq(30 min)		64.3		70.0	

Table	10	Noise	Moni	toring	Results	at NSR1

Remarks:

Unit in dB(A)

Non-Exam - Session that there was non-examination session at NSR1; Limit level = 70.0 dB(A)

Exam – Session that there was examination session at NSR1; Limit level = 65.0 dB(A)

Compliance achieved in the reporting period

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong



NSR7			Fu Cheong	Estate Fu	Yun House		
Date	Monitoring Time Period	Weather Condition	Wind Speed (m/s)	L10(30 min)	L90(30 min)	Leq(30 min)	Limit Level
3/5/2018	07:00-19:00	Sunny	<5	72.6	64.4	70.5	75.0
9/5/2018	15/5/2018 07:00-19:00 Sunny		<5	72.5	65.7	70.5	75.0
15/5/2018			<5	73.0	65.2	70.8	75.0
21/5/2018			<5	73.2	64.5	71.1	75.0
26/5/2018	07:00-19:00	Sunny	<5	72.7	65.0	70.6	75.0
	Average Le	q(30 min)			70.7		75.0

Table 11 Noise Monitoring Results at NSR7

Remarks:

Unit in dB(A)

Limit Level for NSR7 = 75.0 dB(A)

Compliance achieved in the reporting period

- 7.3 The minimum and maximum noise level measure in a single 30-min period at the Sir Ellis Kadoorie Secondary School (NSR1) was 62.7 dB(A) $L_{eq(30min)}$ and 65.7 dB(A) $L_{eq(30min)}$ respectively with an average of 64.3 dB(A) $L_{eq(30min)}$. Therefore, the results were not considered as exceedance. ($L_{eq(30min)}$ no greater than 70.0 dB(A)).
- 7.4 The minimum and maximum noise levels measured in a single 30-min period at the Fu Cheong Estate Fu Yun House (NSR7) were 68.6 dB(A) $L_{eq(30min)}$ and 73.3 dB(A) $L_{eq(30min)}$ respectively with an average of 70.7 dB(A) $L_{eq(30min)}$. Therefore, the results were not considered as exceedance. ($L_{eq(30min)}$ not greater than 75.0 dB(A)).
- 7.5 Backfilling works was undertaken on-site and this was identified as the major influencing factors affecting the monitoring results.





8.0 Non-compliance, Complaints, Notifications of Summons and

Status of Prosecutions

Record on Non-compliance of Action and Limit Levels

8.1 For construction noise, no Action and Limit Level exceedance was recorded at all monitoring stations in the reporting period.

Record on Environmental Complaints Received

- 8.2 No environmental compliant was recorded in the reporting month.
- 8.3 The cumulative statistics on complaints were provided in **Appendix K**.

Record on Notifications of Summons and Successful Prosecution

8.4 No notification of summons or successful prosecution was received this month. The cumulative statistics on notifications of summons and successful prosecutions were provided in **Appendix K**.

Review of Reasons for and Implications of Non-compliance, Complaints, Summons and Prosecutions

8.5 As no notification of summon or successful prosecution was received, the associated review was not required.

Follow-up Actions Taken

8.6 As no notification of summons or successful prosecution was received, the associated follow-up action was not required.





9.0 Forecast of Works Programme and Future Key Issues

- 9.1 The major site work scheduled to be commissioned in the coming three months include:
 - R.C. Frame works;
 - Plumbing installation works;
 - Drainage installation works;
 - Electrical installation works;
 - MVAC installation works;
 - Fire services installation works;
 - Site works of aluminum window / louvre and curtain wall;
 - Grasscrete works;
 - Internal finishing works;
 - Mechanical handling and lifting installation works;
 - Lift services works;
 - Roofing works;
 - Sanitary fitting installation works;
 - External and landscaping works;
 - Soft Landscaping; and
 - Glazing works.
- **9.2** Key issues to be considered in the coming three months include:
 - Properly store and label oils and chemicals on site;
 - Chemical, chemical waste and waste management;
 - Sorting, recycling, storage and disposal of general refuse and construction waste;

EEM

- Properly maintain all drainage facilities and wheel washing facilities on site;
- Generation of dust from construction works;
- Noise impact from operation equipment and machinery on site;
- Generation of site surface runoffs and wastewater from activities on site; and
- Tree protective measures for all retained trees should be well maintained.
- 9.3 The environmental site inspection and environmental monitoring will be continued in the coming month. Impact monitoring for noise in accordance with the approved EM&A Manual has commenced since 4^{th} March 2016. The tentative monitoring schedule is appended in *Appendix G*.

10.0 Solid and Liquid Waste Management Status

- 10.1 The contractor has registered as chemical waste producers for the Contract. C&D material sorting was carried out on site. Sufficient numbers of receptacles were available for general refuse collection.
- 10.2 As advised by the Contractor, 124.83 tons excavated C&D materials were disposed at public fills during the reporting period and 257.18 tons of general refuse was disposed at NENT landfill. No recyclable (e.g. metals, paper/cardboard packaging or plastics) was collected by recycling contractor in the reporting month. 0 tons of inert C&D materials were reused on site and reused in NENT for backfilling purpose respectively. 0 tons of chemical waste was collected by licensed contractor in the reporting period. Monthly Waste Flow Table is given in *Appendix L*.
- 10.3 The Contractor was advised to maintain on site waste sorting and recording system and maximize reused / recycle of C&D wastes.





11.0 Comments, Recommendations and Conclusions

- 11.1 Environmental impact monitoring had been carried out for FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot, Yen Ming Road, West Kowloon Reclamation Area.
- 11.2 The recommended mitigation measures are summarized as below:

Chemical Waste and Waste Management

- C&D material should be sorted and removed timely;
- All plants on site should be properly maintained to prevent oil leakage;
- General refuse and construction waste shall be sorted, recycled, stored and disposed properly and record shall be kept; and
- Larger chemical waste storage tanks shall be provided.

Water Quality Impact

- All drainage facilities on site shall be properly maintained; and
- Generation of site surface runoffs and wastewater from activities on site shall be properly treated with the on-site wastewater treatment system prior to discharge.

Air Quality Impact

- All vehicle should be washed to remove any dusty;
- Haul roads should be sufficiently dampened to minimize fugitive dust generation; and
- Wheel washing facilities shall be installed since water jet is implemented as temporary measures.

Construction Noise Impact

- Noisy operations should be oriented to a direction away from sensitive receivers as far as possible; and
- Noise barrier should be properly implemented during construction work.





Landscape and Visual Impact

- Retained tree should be properly fenced off and the working area; and
- Mulching shall be provided to the retained tree.
- 11.3 The mitigation measures had been implemented to minimize the environmental impacts due to the construction of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot, Yen Ming Road, West Kowloon Reclamation Area. The recommended mitigation measures in the EIA process and the EM&A programme were effective in protecting the environment. As such, the environmental performance during the construction phase was considered acceptable.
- 11.4 Impact noise monitoring was conducted at Sir Ellis Kadoorie Secondary School (NSR1) and the Fu Cheong Estate Fu Yun House (NSR7) on 3rd, 9th, 15th, 21st and 26th May 2018.
- 11.5 The minimum and maximum noise level measure in a single 30-min period at the Sir Ellis Kadoorie Secondary School (NSR1) was 62.7 dB(A) $L_{eq(30min)}$ and 65.7 dB(A) $L_{eq(30min)}$ respectively with an average of 64.3 dB(A) $L_{eq(30min)}$. Therefore, the results were not considered as exceedance. ($L_{eq(30min)}$ no greater than 70.0 dB(A)).
- 11.6 The minimum and maximum noise levels measured in a single 30-min period at the Fu Cheong Estate Fu Yun House (NSR7) were 68.6 dB(A) $L_{eq(30min)}$ and 73.3 dB(A) $L_{eq(30min)}$ respectively with an average of 70.7 dB(A) $L_{eq(30min)}$. Therefore, the results were not considered as exceedance. ($L_{eq(30min)}$ not greater than 75.0 dB(A)).





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

- 11.7 Backfilling works was undertaken on-site and this was identified as the major influencing factors affecting the monitoring results.
- 11.8 In the reporting period, no environmental complaint and no notification of summons or successful prosecution was received.
- 11.9 Weekly construction phase site inspections and landscape and visual impact inspections were conducted during the reporting month as required. The monitoring results and statistics of non-compliance indicated that the EIA process with its recommended mitigation and EM&A programme were effective for protection of the environment and there was no significantly unacceptable environmental impact posed by the Project.
- 11.10 In the reporting month, 124.83 tons excavated C&D materials were disposed at public fills and 257.18 tons of general refuse was disposed at NENT landfill. No recyclable (e.g. metals, paper/cardboard packaging or plastics) was collected by the recycling contractor.
- 11.11 Construction activities to be undertaken in the next three months include R.C. Frame works, plumbing installation works, drainage installation works, electrical installation works, MVAC installation works, fire services installation works, site works of aluminum window / louvre and curtain wall, grasscrete works, internal finishing works, mechanical handling lifting installation works, lift services works, roofing works, sanitary fitting installation works and external and landscaping works. Potential environmental impacts include generation of various wastes including oil and chemical wastes, general refuse and construction waste, maintenance work to all drainage facilities and wheel washing facility, dust from construction works, waste water from surface runoff, drainage facilities and wheel washing facilities noise from operation equipment and machinery, tree protective measures shall be carried for tree retained.
- 11.12 The Contractor should properly implement environmental mitigation measures as per the implementation schedule in the EM&A manual to ensure no adverse environmental impacts to be arisen from the construction works. The Contractor is also reminded to maintain good housekeeping at the site.

Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Appendix A Master Programme






China Road and Bridge Corporation

Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

Mile P	ntract period Project commencement	997 days	Wed 9/12/15	Fri 31/8/18											
Mile F	Project commencement		MI- LOROISE	141-1-0/10/11-	9/12	9/12		I.		1		1	l .	L	1
Mile	Project completion	1 day 1 day	Wed 9/12/15 Fri 31/8/18	Wed 9/12/15 Fri 31/8/18	9/12	9/12						1			
P	lestone Dates	997 days	Wed 9/12/15	Fri 31/8/18		-		-					1		
	Project commencement	1 day	Wed 9/12/15	Wed 9/12/15	9/12	9/12							1		
	Submission / Application of Form WWO 046 (Part	1 day	Wed 22/3/17	Wed 22/3/17	1							¢ 22/3			
	I & II) Submission of Form WWO46 Part IV	1 day	Wed 11/7/18	Wed 11/7/18	1					1					1
	Last Manhole Connection Completion	1 day	Mon 30/4/18	Mon 30/4/18	į										
V	Water Certificate Obtained (Plumbing Installation)	1 day	Wed 18/7/18	Wed 18/7/18	1										
	Handover of Transformer Room & Switch Room	1 day	Tue 2/1/18	Tue 2/1/18	1					1					
	to CLP Power Energisation	1 day	Sat 21/7/18	Sat 21/7/18	i i										
	Lift certificate Obtained (Fireman's Lift)	1 day	Mon 23/7/18	Mon 23/7/18	1										
3 F	Form 501 Submission	1 day	Thu 12/7/18	Thu 12/7/18	1								1		
	FSD inspection	1 day	Thu 2/8/18	Thu 2/8/18	i i							1			
	F.S. Certificate Obtained	1 day	Wed 22/8/18	Wed 22/8/18	1								1	1	1
	Site Handover itical Path Summary	1 day 997 days	Fri 31/8/18 Wed 9/12/15	Fri 31/8/18 Fri 31/8/18	ļ			1		1		1			1
0	Project commencement	0 days	Wed 9/12/15	Wed 9/12/15	k	9/12						1	1	I I	
	Hoarding installation	113 days	Thu 10/12/15	Thu 31/3/16	10/12	*	31/3								
	H-pile (305x305x180) - total 399nos	127 days	Fri 1/4/16	Fri 5/8/16			1/4		5/8						
	As-built record submission and selection of	14 days	Sat 6/8/16	Fri 19/8/16					6/8 19/8						
-	loading test (70% completed)	38 days	Sat 20/8/16	Mon 26/9/16					20/8	26/9					
_	Loading test (70% completed) Construction of Pile cap with sheetpile (80%	38 days 184 days	Tue 27/9/16	Wed 29/3/17	1		I	i	20,0 27/			29	/3		
C	Completed)				1			I I							
1 B	Backfilling works for Pile Cap	45 days	Thu 30/3/17	Sat 13/5/17				I.				30/3 🎽	13/5		
	R.C. Frame of A2 (G.L.1-4/A-F), G/F~UR/F,	335 days	Sun 14/5/17	Fri 13/4/18				I.		i I			14/5		1
	External Wall Preparation Works for Curtain Wall Installation CW1, CW2	30 days	Sat 14/4/18	Sun 13/5/18	1		1	1					1	1	1
	Erection of Aluminium Frames (CW1, CW2)	31 days	Mon 14/5/18	Wed 13/6/18	1			Ì							
3 (Glazing works	21 days	Thu 14/6/18	Wed 4/7/18											
	Removal of scaffoldings	28 days	Thu 5/7/18	Wed 1/8/18	1								1		
	FSD inspection and Issuance of FS Certificate	21 days	Thu 2/8/18	Wed 22/8/18	i										i i
-	SCCU Inspection General cleaning	8 days 1 day	Thu 23/8/18 Fri 31/8/18	Thu 30/8/18 Fri 31/8/18											
	eparation works	365 days	Thu 10/12/15	Thu 8/12/16	ł			_							1
	Mobilization	7 days	Thu 10/12/15	Wed 16/12/15		16/12				1		1			
	Condition survey and U/G utility survey	80 days	Thu 10/12/15	Sat 27/2/16	10/12										
	Setting up site office (1) Drawing submission and	130 days	Thu 10/12/15	Sun 17/4/16	10/12		17/4								
	approval Setting up site office (2) Material fabrication and	60 days	Mon 18/4/16	Thu 16/6/16	1		18/4	16/6					 		
	construction	00 0233	10101110/4/10	1110 10/0/10	1									1	1
	Temporary electricity and water	218 days	Thu 10/12/15	Thu 14/7/16	10/12				14/7	Ì					i
	Setting out of site area	66 days	Thu 10/12/15	Sat 13/2/16	10/12		21/2								1
	Hoarding (1) installation	113 days	Thu 10/12/15	Thu 31/3/16	10/12		31/3 1/4 30	/5						1	1
	Hoarding (2) painting and lighting Removal of existing trees	60 days 60 days	Fri 1/4/16 Thu 10/12/15	Mon 30/5/16 Sun 7/2/16	10/12	7/2	00,								
	Hoarding enhancement work	45 days	Tue 25/10/16	Thu 8/12/16	1					25/10	8/12			1	1
	ling work	446 days	Wed 9/12/15	Sun 26/2/17		-									
5 C	Design Submission	78 days	Wed 9/12/15	Wed 24/2/16	0/12	4/1						1			
7	Preparation and submit piling design Review of piling design by SCU	27 days 30 days	Wed 9/12/15 Tue 5/1/16	Mon 4/1/16 Wed 3/2/16	9/12	5/1 3/2							1		
3	Coordination with MTRC and Method statement	21 days	Thu 4/2/16	Wed 3/2/16 Wed 24/2/16		4/2 24/2				1			1		
	for MTRC Approval	21 ddjo	1110 112110	1100 2 1121 10								1	1	l I	
	Noise permit application	45 days	Mon 14/12/15	Wed 27/1/16	14/1	2 27/1									
D N	Material testing	141 days	Mon 28/12/15	Mon 16/5/16	į	28/12 11/1		1		1			1		
2	H-Pile Delivery (Batch 1 to 4) H-Pile Delivery (Batch 5)	15 days 1 day	Mon 28/12/15 Tue 12/4/16	Mon 11/1/16 Tue 12/4/16	1		12/4 12/4	I.		i I			1		
3	H-Pile Delivery (Batch 6)	1 day	Wed 13/4/16	Wed 13/4/16	1		13/4 13/4	1		1			1		1
4	Delivery of Splicing Steel Plate (1st Batch)	1 day	Sun 21/2/16	Sun 21/2/16	1	21/2 <u>21/2</u>		i.					1		
5	Delivery of Splicing Steel Plate (2nd Batch)	1 day	Mon 9/5/16	Mon 9/5/16			9/5 9/5 10/5 516/5	I I					1		
5	Material Testing for H-pile (Batch 1)	7 days	Tue 10/5/16	Mon 16/5/16	1	28/1	10/5	1		l l			1	1	1
	Material Testing for H-pile (Batch 2, 3 & 4 & Batch 1 16mmthk, steel plate)	15 days	Thu 28/1/16	Thu 11/2/16	i			i.							
3	Material Testing for H-pile (Batch 5, 6 & Batch	13 days	Fri 22/4/16	Wed 4/5/16	1		22/44/5	I					1		
	2, 16mm thk steel plate)	-			ļ	\perp		I.					1		
9 C	Completion of monitoring check points, noise	30 days	Mon 8/2/16	Tue 8/3/16		8/2	3/3	I I					1		
	barrier and baseline noise monitoring	104 dour	The 10/2/1/	Tuo 21///1/	1	_		ا بور		l I			1		
1 II	Installation of trial pile (2 hammers) Trial pile driving (21 nos.)	104 days 71 days	Thu 10/3/16 Thu 10/3/16	Tue 21/6/16 Thu 19/5/16		10/3	19/5	Ĩ					1		
2	PDA test	1 day	Fri 20/5/16	Fri 20/5/16			20/5 20/5	1					1		
3	Final set table preparation	1 day	Tue 31/5/16	Tue 31/5/16			31/5 31						1		1
4	Approval of Hiley Formula Data and Final Set	21 days	Wed 1/6/16	Tue 21/6/16	1		1/6 🎽	21/6							
5 lr	Table Installation of working pile	332 days	Fri 1/4/16	Sun 26/2/17	1					1		· · · · · · · · · · · · · · · · · · ·	1		
, II ;	Pile driving	332 days 127 days	Fri 1/4/16 Fri 1/4/16	Sun 26/2/17 Fri 5/8/16	į							· · · · · ·	1		
7	H-pile (305x305x180) - total 399nos	127 days	Fri 1/4/16	Fri 5/8/16	1		1/4	1	5/8	i I					
3	H-pile (305x305x223) - total 87nos	48 days	Sat 21/5/16	Thu 7/7/16	1		21/5	7,	/7	1			1		1
9	Final set	39 days	Wed 22/6/16	Sat 30/7/16	i			2/6	30/7						i
) L	PDA test	60 days	Wed 22/6/16	Sat 20/8/16	1		2	2/0 	6/8 19/8	1			1		
	As-built record submission and selection of loading test	14 days	Sat 6/8/16	Fri 19/8/16	1			I I	-,-				1		
2	Loading test (including set up)*	38 days	Sat 20/8/16	Mon 26/9/16	1			i I	20/8	26/9					
		Critical Path	Progress			one Summary									

7-13 Feb 2016 and 27 Jan- 2 Feb 2017 and 16 Feb - 19 Feb 2018 Chinese New Year site close

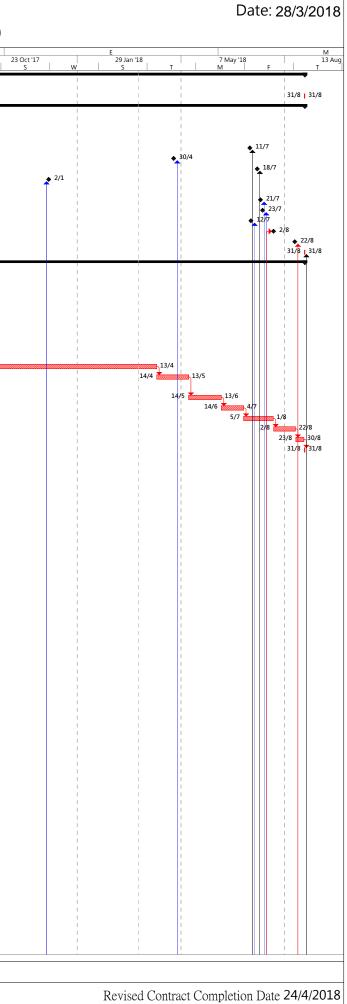


China Road and Bridge Corporation

Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

est for FD3-P11 est for FC7-P4 PDA test and CAPWAP analysis , FA7-P2, FA7-P3 (PDA test and CAPWAP analysis , FA7-P2, FA7-P3 (2nd time) ing Work for FA7 work for FA7 work for FA7 (Revised Design) f tower crane proposal tower crane proposal tower crane 0 1, TC2 of tower crane TC1 & TC2 tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval to p Pile cap with sheetpile(G.L. an of Pile cap with sheetpile(G.L. an of Pile cap with open cut method usorks for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/ F-K) of Pile cap FA7 (including and the for Pile cap to G/F Beam	4 days 4 days 4 days 7 days 54 days 7 days 54 days 1 day 763 days 32 days 1 day 87 days 40 days 30 days 14 days 30 days 14 days 40 days 32 days 40 days 32 days 86 days 540 days 184 days 175 days 356 days 23 days 23 days 40 days 175 days 356 days 23 days 23 days 40 days 175 days 356 days 356 days 356 days 356 days 34 days 175 days 356 days 356 days 34 days 40 days 175 days 356 days 34 days 40 days 356 days 34 days 40 days 34 days 175 days 356 days 34 days 34 days 40 days 34 days 34 days 40 days 34 days 40 days 34 days 40 days 4	Tue 6/12/16 Tue 13/12/16 Tue 25/10/16 Wed 2/11/16 Thu 17/11/16 Thu 24/11/16 Tue 26/4/16 Tue 26/4/16 Tue 9/8/16 Tue 9/8/16 Mon 14/11/16 Mon 14/11/16 Mon 14/11/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Sat 22/4/17 Sat 22/4/17 Sat 22/4/17 Sat 22/4/17	Fri 9/12/16 Fri 16/12/16 Fri 28/10/16 Fri 28/10/16 Fri 4/11/16 Mon 16/1/17 Sun 26/2/17 Mon 28/5/18 Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Fri 23/12/16 Mon 13/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Wed 19/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18 Wen 27/3/18
PDA test and CAPWAP analysis , FA7-P2, FA7-P3 PDA test and CAPWAP analysis , FA7-P2, FA7-P3 (not cap work for FA7 work for FA7 work for FA7 (Revised Design) f tower crane proposal f tower crane proposal f tower crane Proposal f tower crane TC1 & TC2 tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/A-F) on of Pile cap FA7 (including or pile cap to G/F Beam	4 days 3 days 7 days 54 days 41 days 763 days 32 days 1 day 87 days 30 days 14 days 741 days 741 days 40 days 30 days 14 days 741 days 86 days 540 days 184 days 81 days 23 days 24 days 175 days 356 days 23 days 22 days 90 days 34 days 34 days 34 days 39 days 199 days 199 days 199 days	Tue 25/10/16 Wed 2/11/16 Thu 17/11/16 Tue 17/1/17 Tue 26/4/16 Tue 9/8/16 Tue 9/8/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Sun 28/1/18 Wed 22/2/17	Fri 28/10/16 Fri 4/11/16 Mon 16/1/17 Sun 26/2/17 Mon 28/5/18 Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Won 18/4/16 Mon 13/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
, FA7-P2, FA7-P3 PDA test and CAPWAP analysis , FA7-P2, FA7-P3 (2nd time) ing Work for FA7 work for FA7 work for FA7 (Revised Design) f tower crane proposal t ower crane proposal t ower crane TC1 & TC2 tower crane TC1 & TC2 tower crane a cap submission and PTS approval cap - Review and approval by SCU ubmission and approval of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. 5-9/ F-K) 5-9/ F-K) 5-9/ F-K) 5-9/ F-K) of Pile cap FA7 (including cap of Pile cap to G/F Beam	3 days 7 days 54 days 41 days 763 days 32 days 1 day 87 days 40 days 30 days 14 days 741 days 741 days 40 days 32 days 86 days 540 days 184 days 81 days 22 days 22 days 22 days 22 days 22 days 22 days 34 days 356 days 23 days 24 days 34 days 354 days 355 days 354 days 354 days 355 days 354 days 354 days 354 days 354 days 355 days 354 days 355 days 354 days 354 days 354 days 355 days 354 days 354 days 355 days 354 days 355 days 354 days 355 days 355 days 355 days 356 days 356 days 357	Wed 2/11/16 Thu 17/11/16 Thu 24/11/16 Tue 2/1/17 Tue 26/4/16 Tue 26/4/16 Tue 26/4/16 Tue 26/4/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 2/2/4/17 Sun 28/1/18 Wed 22/2/17	Fri 4/11/16 Wed 23/11/16 Mon 16/1/17 Sun 26/2/17 Mon 28/5/18 Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Won 18/4/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
PDA test and CAPWAP analysis , FA7-P2, FA7-P3 (2nd time) ing Work for FA7 work for FA7 work for FA7 (Revised Design) f tower crane proposal tower crane proposal tower crane rorposal tower crane TC1 & TC2 for tower crane TC1 & TC2 tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval to file caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. an of Pile cap with sheetpile(G.L. an of Pile cap with sheetpile(G.L. to file cap with sheetpile(G.L. to file cap with open cut method to file cap with open cut method to file cap with open cut method to file cap FA7 (including e orks for Pile cap to G/F Beam	7 days 54 days 41 days 763 days 32 days 1 day 87 days 40 days 30 days 14 days 741 days 741 days 32 days 86 days 540 days 184 days 81 days 356 days 23 days 22 days 90 days 52 days 352 days 34 days 34 days 394 days	Thu 17/11/16 Thu 24/11/16 Tue 17/1/17 Tue 26/4/16 Tue 9/8/16 Mon 14/11/16 Tue 9/8/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Sun 28/1/18 Wed 22/2/17	Wed 23/11/16 Mon 16/1/17 Sun 26/2/17 Mon 28/5/18 Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Won 13/6/16 Thu 30/6/16 Thu 30/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
, FA7-P2, FA7-P3 (2nd time) ing Work for FA7 work for FA7 work for FA7 (Revised Design) f lower crane proposal t ower crane proposal t ower crane proposal t ower crane TC1 & TC2 of tower crane TC1 & TC2 lower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval to of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. an of Pile cap with sheetpile(G.L. an of pile cap with sheetpile(G.L. an of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	7 days 54 days 41 days 763 days 32 days 1 day 87 days 40 days 30 days 14 days 741 days 741 days 32 days 86 days 540 days 184 days 81 days 356 days 23 days 22 days 90 days 52 days 352 days 34 days 34 days 394 days	Thu 17/11/16 Thu 24/11/16 Tue 17/1/17 Tue 26/4/16 Tue 9/8/16 Mon 14/11/16 Tue 9/8/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Sun 28/1/18 Wed 22/2/17	Wed 23/11/16 Mon 16/1/17 Sun 26/2/17 Mon 28/5/18 Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Won 13/6/16 Thu 30/6/16 Thu 30/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
ing Work for FA7 work for FA7 work for FA7 (Revised Design) f tower crane proposal tower crane proposal tower crane TC1 & TC2 of tower crane TC1 & TC2 tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/A-F) or Pile cap FA7 (including orks for Pile cap to G/F Beam	54 days 41 days 763 days 32 days 1 day 87 days 30 days 30 days 14 days 741 days 741 days 741 days 32 days 86 days 540 days 184 days 81 days 356 days 23 days 22 days 22 days 22 days 90 days 52 days 34 days 34 days 394 days	Thu 24/11/16 Tue 17/1/17 Tue 26/4/16 Tue 26/4/16 Tue 26/4/16 Tue 9/8/16 Mon 14/11/16 Mon 14/11/16 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Sun 28/1/18 Wed 22/2/17	Mon 16/1/17 Sun 26/2/17 Mon 28/5/18 Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Mon 13/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
work for FA7 (Revised Design) f tower crane proposal tower crane proposal tower crane 1, TC2 f tower crane 1, TC2 f tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval f of pile caps (ELS in Two Stage) n of Pile cap with sheetpile(G.L. an of Pile cap with sheetpile(G.L. an of pile cap with open cut method works for Pile Cap 1-5/F-K) 5-9/F-K) 5-9/F-K) 5-9/F-K) f of Pile cap FA7 (including cap orks for Pile cap to G/F Beam	41 days 763 days 32 days 1 day 87 days 30 days 14 days 741 days 40 days 32 days 86 days 540 days 184 days 175 days 356 days 23 days 22 days 22 days 90 days 52 days 34 days 394 days 199 days	Tue 17/1/17 Tue 26/4/16 Tue 26/4/16 Tue 9/8/16 Mon 14/11/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 2/2/1/18 Wed 22/2/17 Sat 22/4/17	Sun 26/2/17 Mon 28/5/18 Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Mon 18/4/16 Mon 13/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
f tower crane proposal t ower crane proposal t ower crane 1, TC2 of tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval to of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. on of Pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/A-F) on of Pile cap FA7 (including e orks for Pile cap to G/F Beam	763 days 32 days 1 day 87 days 40 days 30 days 14 days 741 days 40 days 32 days 86 days 540 days 184 days 81 days 175 days 22 days 90 days 52 days 90 days 52 days 34 days 408 days 199 days	Tue 26/4/16 Tue 2/4/16 Tue 9/8/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Wed 6/4/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 32/1/18 Wed 22/2/17 Sat 22/4/17	Mon 28/5/18 Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Mon 18/4/16 Mon 13/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
tower crane proposal tower crane 1, TC2 of tower crane TC1 & TC2 tower crane TC1 & TC2 tower crane TC1 & TC2 tower crane cap submission and PTS approval cap submission and approval of pile caps (ELS in Two Stage) on of Pile caps (ELS in Two Stage) on of Pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. 1-5/- K.) 1-5/- F.K) 1-5/- F.K) 5-9/ F-K) 5-9/ F-K) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	32 days 1 day 87 days 40 days 30 days 14 days 741 days 40 days 32 days 86 days 540 days 184 days 81 days 175 days 23 days 22 days 22 days 90 days 356 days 23 days 22 days 34 days 34 days 34 days 39 days 199 days 199 days	Tue 26/4/16 Tue 9/8/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Fri 27/5/16 Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Mon 18/4/16 Mon 13/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
tower crane proposal tower crane 1, TC2 of tower crane TC1 & TC2 tower crane TC1 & TC2 tower crane TC1 & TC2 tower crane cap submission and PTS approval cap submission and approval of pile caps (ELS in Two Stage) on of Pile caps (ELS in Two Stage) on of Pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. 1-5/- K.) 1-5/- F.K) 1-5/- F.K) 5-9/ F-K) 5-9/ F-K) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	1 day 87 days 40 days 30 days 14 days 741 days 40 days 32 days 86 days 540 days 184 days 81 days 23 days 22 days 22 days 22 days 90 days 52 days 34 days 34 days 394 days 199 days	Tue 9/8/16 Mon 14/11/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Thu 10/3/16 Firi 13/5/16 Wed 6/4/16 Tue 27/9/16 Sun 29/1/17 Sun 29/1/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 38/5/17 Sun 28/1/18 Wed 22/2/17	Tue 9/8/16 Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Mon 18/4/16 Mon 13/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
tower crane 1, TC2 of tower crane TC1 & TC2 tower crane TC1 & TC2 tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval of pile caps (ELS in Two Stage) in of Pile cap with sheetpile(G.L. an of pile cap with sheetpile(G.L. an of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/A-F) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	87 days 40 days 30 days 14 days 741 days 40 days 32 days 86 days 540 days 184 days 81 days 175 days 23 days 22 days 90 days 52 days 34 days 408 days 394 days 199 days	Mon 14/11/16 Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Thu 10/3/16 Thu 10/3/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Sun 28/1/18 Wed 22/2/17	Wed 8/2/17 Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Mon 13/6/16 Tuu 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
1, TC2 of tower crane TC1 & TC2 tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. on of Pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/F-K) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	40 days 30 days 14 days 741 days 40 days 32 days 86 days 540 days 184 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 34 days 408 days 394 days	Mon 14/11/16 Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 32/4/17 Wed 22/2/17 Sat 22/4/17	Fri 23/12/16 Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Mon 18/4/16 Mon 13/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
of tower crane TC1 & TC2 tower crane cap submission and PTS approval cap - Review and approval by SCU ubmission and approval of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. on of Pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/ F-K) 5-9/ F-K) of Pile cap FA7 (including orks for Pile cap to G/F Beam	30 days 14 days 741 days 40 days 32 days 86 days 540 days 184 days 81 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 394 days 199 days	Tue 10/1/17 Tue 15/5/18 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Thu 38/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Wed 8/2/17 Mon 28/5/18 Tue 20/3/18 Mon 18/4/16 Mon 13/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
tower crane a cap submission and PTS approval a cap - Review and approval by SCU ubmission and approval n of pile caps (ELS in Two Stage) n of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. n of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/F-K) 5-9/F-K) 5-9/F-K) 5-9/F-K) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	14 days 741 days 40 days 32 days 86 days 184 days 81 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 394 days 199 days	Tue 15/5/18 Thu 10/3/16 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Wed 22/2/17 Sat 22/4/17	Mon 28/5/18 Tue 20/3/18 Mon 18/4/16 Mon 13/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
cap submission and PTS approval cap - Review and approval by SCU ubmission and approval o of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. on of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/A-F) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	741 days 40 days 32 days 86 days 540 days 184 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 408 days 394 days 199 days	Thu 10/3/16 Thu 10/3/16 Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Wed 22/2/17 Sat 22/4/17	Tue 20/3/18 Mon 18/4/16 Mon 13/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
cap - Review and approval by SCU ubmission and approval of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. on of Pile cap with open cut method works for Pile Cap 1-5/-K) 1-5/-K) 5-9/-F,K) 5-9/-F,K) 5-9/-F,K) 5-9/-F,K) of Pile cap FA7 (including or shor Pile cap to G/F Beam	40 days 32 days 86 days 540 days 184 days 81 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 34 days 394 days 199 days	Fri 13/5/16 Wed 6/4/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Mon 13/6/16 Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
ubmission and approval of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. on of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/F-K) 5-9/F-K) of Pile cap FA7 (including orks for Pile cap to G/F Beam	86 days 540 days 184 days 81 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 394 days 199 days	Wed 6/4/16 Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Thu 30/6/16 Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
n of pile caps (ELS in Two Stage) on of Pile cap with sheetpile(G.L. on of Pile cap with sheetpile(G.L. on of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/F-K) 5-9/F-K) 5-9/F-K) of Pile cap FA7 (including orks for Pile cap to G/F Beam	540 days 184 days 81 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 408 days 199 days 199 days	Tue 27/9/16 Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Tue 20/3/18 Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
n of Pile cap with sheetpile(G.L. n of Pile cap with sheetpile(G.L. n of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/ A-F) n of Pile cap FA7 (including e orks for Pile cap to G/F Beam	184 days 81 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 408 days 394 days 199 days	Tue 27/9/16 Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Wed 29/3/17 Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
on of Pile cap with sheetpile(G.L. on of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/A-F) of Pile cap FA7 (including orks for Pile cap to G/F Beam	81 days 175 days 356 days 23 days 22 days 90 days 52 days 34 days 394 days 199 days	Sun 29/1/17 Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Wed 19/4/17 Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
on of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/F-K) 5-9/A-F) n of Pile cap FA7 (including orks for Pile cap to G/F Beam	175 days 356 days 23 days 22 days 90 days 52 days 34 days 408 days 394 days 199 days	Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
on of pile cap with open cut method works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/F-K) 5-9/A-F) n of Pile cap FA7 (including orks for Pile cap to G/F Beam	175 days 356 days 23 days 22 days 90 days 52 days 34 days 408 days 394 days 199 days	Sat 4/2/17 Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Fri 28/7/17 Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/A-F) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	356 days 23 days 22 days 90 days 52 days 34 days 394 days 199 days	Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
works for Pile Cap 1-5/F-K) 1-5/A-F) 5-9/F-K) 5-9/A-F) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	356 days 23 days 22 days 90 days 52 days 34 days 394 days 199 days	Thu 30/3/17 Thu 30/3/17 Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Tue 20/3/18 Fri 21/4/17 Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
1-5/ A-F) 5-9/ F-K) 5-9/ A-F) of Pile cap FA7 (including e orks for Pile cap to G/F Beam	23 days 22 days 90 days 52 days 34 days 408 days 394 days 199 days	Sat 22/4/17 Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Sat 13/5/17 Tue 15/8/17 Tue 20/3/18
5-9/ F-K) 5-9/ A-F) n of Pile cap FA7 (including e e orks for Pile cap to G/F Beam	90 days 52 days 34 days 408 days 394 days 199 days	Thu 18/5/17 Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Tue 15/8/17 Tue 20/3/18
5-9/ A-F) n of Pile cap FA7 (including e orks for Pile cap to G/F Beam	52 days 34 days 408 days 394 days 199 days	Sun 28/1/18 Wed 22/2/17 Sat 22/4/17	Tue 20/3/18
n of Pile cap FA7 (including e orks for Pile cap to G/F Beam	34 days 408 days 394 days 199 days	Wed 22/2/17 Sat 22/4/17	
orks for Pile cap to G/F Beam	408 days 394 days 199 days	Sat 22/4/17	1011111111111111
orks for Pile cap to G/F Beam	394 days 199 days		
orks for Pile cap to G/F Beam	394 days 199 days		Sun 3/6/18
	199 days	Jat 22/4/17	Sun 20/5/18
	20 days	Sat 22/4/17	Mon 6/11/17
1-4/F-K)		Sat 22/4/17	Sat 20/5/17
1-4/A-F)	48 days	Sun 14/5/17	Fri 30/6/17
4-7/ F-K)	29 days	Fri 26/5/17	Fri 23/6/17
7-9/F-K)	29 days	Sat 1/7/17	Sat 29/7/17
G.L.6-9/ E-F) 4-7/ A-F)	40 days 19 days	Sun 30/7/17 Fri 8/9/17	Thu 7/9/17 Tue 26/9/17
4-7/ A-F) 7-9/ A-F)	41 days	Wed 27/9/17	Mon 6/11/17
include backfill from G/F Beam to	367 days	Fri 19/5/17	Sun 20/5/18
ilab)			
1-4/F-K)	30 days	Fri 19/5/17	Sat 17/6/17
G.L.1-9/A-K)	120 days	Sun 21/1/18	Sun 20/5/18
F	188 days	Thu 1/6/17	Tue 5/12/17
1-3/F-K)	43 days	Thu 1/6/17	Thu 13/7/17
1-3/A-F) 4-5/ F-K)	26 days 27 days	Sat 1/7/17 Sat 22/7/17	Wed 26/7/17 Thu 17/8/17
3-5/ A-F)	27 days 26 days	Mon 7/8/17	Fri 1/9/17
8-9/ F-K)	71 days	Mon 21/8/17	Mon 30/10/17
G.L.6-9/ E-F)	15 days	Tue 12/9/17	Tue 26/9/17
7-9/ A-F)	29 days	Tue 7/11/17	Tue 5/12/17
ks	30 days	Sun 24/9/17	Mon 23/10/17
ank (G.L.4-5/F-K)	30 days	Sun 24/9/17	Mon 23/10/17
F to 1/F	164 days	Thu 20/7/17	Sat 30/12/17
			Thu 31/8/17 Mon 11/9/17
			Mon 11/9/17 Mon 23/10/17
			Wed 15/11/17
			Sat 23/12/17
G.L.3-6/ E-F)	21 days	Wed 27/9/17	Tue 17/10/17
7-9/ A-F)	25 days	Wed 6/12/17	Sat 30/12/17
	143 days	Mon 4/9/17	Wed 24/1/18
1-4/F-K)	36 days	Mon 4/9/17	Mon 9/10/17
	38 days		Fri 3/11/17
			Sat 16/12/17
			Wed 29/11/17 Sat 2/12/17
			Sat 2/12/17 Wed 17/1/18
			Wed 24/1/18
<i>[]</i> // []			Tue 13/2/18
1-4/F-K)	63 days	Tue 10/10/17	Mon 11/12/17
1-4/A-F)	48 days	Sat 4/11/17	Thu 21/12/17
4-7/ F-K)	18 days	Sun 17/12/17	Wed 3/1/18
			Wed 10/1/18
4-7/ A-F)			Tue 6/2/18
4-7/ A-F) 7-9/ F-K)			Tue 13/2/18 Sat 17/3/18
4-7/ A-F) 7-9/ F-K) 7-9/ A-F)			Sat 17/3/18 Sat 27/1/18
4-7/ A-F) 7-9/ F-K) 7-9/ A-F)			Thu 8/2/18
4-7/ A-F) 7-9/ F-K) 7-9/ A-F) 1-4/F-K)		Wed 7/2/18	Fri 9/3/18
4-7/ A-F) 7-9/ F-K) 7-9/ A-F)	31 days	Wed 14/2/18	Sat 17/3/18
4-7/ A-F) 7-9/ F-K) 7-9/ A-F) 1-4/F-K) 1-4/A-F)	31 days 32 days		Mi
4-7/ A-F) 7-9/ F-K) 7-9/ A-F) 1-4/F-K) 1-4/A-F) 7-9/ F-K) 7-9/ F-K)	32 days	Progress	Mi
	1-3/F-K) 1-3/A-F) 4-7/F-K) 3-5/A-F) 7-9/F-K) 1-4/A-F) 4-7/F-K) 1-4/A-F) 4-7/F-K) 1-4/A-F) 1-4/A-F) 1-4/A-F) 1-4/A-F) 1-4/F-K) 1-4/A-F) 1-4/A-F) 1-4/A-F) 1-4/A-F) 1-4/A-F) 1-4/A-F) 1-4/A-F) 1-4/A-F) 1-4/A-F)	1-3/F-K) 43 days 1-3/A-F) 47 days 1-3/A-F) 47 days 4-7/ F-K) 37 days 35/A-F) 75 days 7-9/ F-K) 54 days 1-3/A-F) 21 days 1-3/A-F) 21 days 1-4/A-F) 25 days 1-4/A-F) 36 days 1-4/A-F) 38 days 1-1/A-F) 17 days 1-4/A-F) 38 days 1-1/A-F) 17 days 7-9/ F-K) 25 days 1-2/F-K) 54 days 1-1/A-F) 17 days 7-9/ F-K) 25 days 1-2/7 days 1-4/A-F) 1-4/A-F) 18 days 1-4/A-F) 38 days 1-4/F-K) 63 days 1-4/F-K) 18 days 4-7/ A-F) 39 days 7-9/ F-K) 20 days 7-9/ F-K) 20 days 7-9/ A-F) 20 days 7-9/ A-F) 20 days 7-9/ A-F) 20 days	1-3/F-K) 43 days Thu 20/7/17 1-3/A-F) 47 days Thu 27/7/17 1-3/A-F) 47 days Sun 17/9/17 4-7/ F-K) 37 days Sun 17/9/17 55/ A-F) 75 days Sat 2/9/17 7-9/ F-K) 54 days Tue 31/10/17 1-3/A-F) 21 days Wed 27/9/17 7-9/ F-K) 25 days Wed 6/12/17 1-4/F-K) 36 days Mon 4/9/17 1-4/F-K) 36 days Mon 4/9/17 1-4/F-K) 36 days Wed 27/9/17 1-4/F-K) 36 days Wed 71/9/17 1-4/F-K) 36 days Wed 18/10/17 1-4/F-K) 43 days Wed 18/10/17 1-4/F-K) 54 days Tue 24/10/17 1-4/F-K) 17 days Thu 16/11/17 7-9/ F-K) 25 days Sun 31/12/17 7-9/ F-K) 25 days Sun 31/12/17 1-4/F-K) 18 days Sat 4/11/17 1-4/F-K) 18 days Sun 17/12/17 1-4/F-K) 18 days

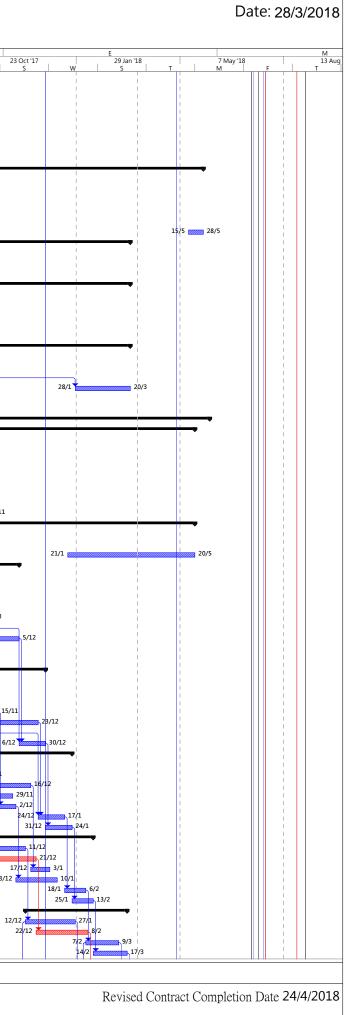


Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

		Start	F	7 Dec '15 T	14 Mar ' S W	s l	20 Jun '16 T M	26 Sep '16 F T	2 Jan '17 S W	S	10 Apr '17 T	M	ul'17 F T
152 4/F to R/F	70 days	Sun 28/1/18	Sat 7/4/18										1
L53 A1 (G.L.1-4/F-K) L54 A2 (G.L.1-4/A-F)	47 days	Sun 28/1/18	Thu 15/3/18			1							
12 (G.E.T 1)/(T)	43 days	Fri 9/2/18	Fri 23/3/18			1							1
No (G.E./ XI II)	20 days	Sat 10/3/18	Thu 29/3/18		1	1			l.				1
A6 (G.L.7-9/ A-F) L57 R/F to UR/F	21 days	Sun 18/3/18 Sat 24/3/18	Sat 7/4/18 Fri 13/4/18			1							
	21 days				i.	i			i	i i			i
Late cast portions (Temp openings for Tower Crane, Material Hoist, Water Tank, etc)	60 days	Thu 5/4/18	Sun 3/6/18										
¹⁵⁹ Material and Shopdrawing submissions for	180 days	Mon 2/10/17	Fri 30/3/18			i i							2/10
mock up items	100 uays	1011 2/10/17	111 30/3/10										1
¹⁶⁰ Sample of finished work	134 days	Mon 15/1/18	Mon 28/5/18										
161 Lavatory	73 days	Mon 22/1/18	Wed 4/4/18		i.	i			i	i i			i i
162 Confirmation of Setting Out	7 days	Mon 22/1/18	Sun 28/1/18										
163 Flooring screeding	7 days	Mon 29/1/18	Sun 4/2/18										
164 Wall and Floor Tiles	10 days	Mon 5/2/18	Wed 14/2/18		1	1				1			1
L65 BS Installation	10 days	Sun 4/3/18	Tue 13/3/18										
L66 Ceiling Installation	3 days	Wed 14/3/18	Fri 16/3/18		i i	i			i	i i			i i
167 Install Sanitary Fitting	3 days	Sat 17/3/18	Mon 19/3/18										
L68 General Cleaning and Inspection of Mock Up	7 days	Thu 29/3/18	Wed 4/4/18										
L69 Locker	80 days	Mon 15/1/18	Wed 4/4/18		1	I.			l.	1			1
L70 Confirmation of Shop Drawing and Colour	30 days	Mon 15/1/18	Tue 13/2/18										
selection	,				i i	i			i				i i
⁷¹ Fabrication	34 days	Wed 14/2/18	Mon 19/3/18			1							
172 Installation	5 days	Tue 20/3/18	Sat 24/3/18						i i				
General Cleaning and Inspection of Mock Up	7 days	Thu 29/3/18	Wed 4/4/18		1	i.			1				i i
174 Changing & Shower Room	74 days	Sun 21/1/18	Wed 4/4/18			1							
L75 Confirmation of Setting Out	7 days	Sun 21/1/18	Sat 27/1/18		i	i			i	- i			
176 Flooring screeding	7 days	Sun 28/1/18	Sat 3/2/18										- ·
177 Wall and Floor Tiles	10 days	Sun 4/2/18	Tue 13/2/18		i I	1							
178 BS Installation	10 days	Wed 14/2/18	Fri 23/2/18		1	1	i		1				í í
179 Ceiling Installation	14 days	Sat 24/2/18	Fri 9/3/18		I I	1			I I				
180 Install Sanitary Fitting	4 days	Sun 18/3/18	Wed 21/3/18		Í.	i			1	- i			- 11 - i -
181 General Cleaning and Inspection of Mock Up 182 Corridor	7 days	Thu 29/3/18	Wed 4/4/18			1			1				
Solitadi	62 days	Mon 12/2/18	Sat 14/4/18		i I				i				
Commuter of County Cut	7 days	Mon 12/2/18	Sun 18/2/18			1	I						1
	7 days	Mon 19/2/18 Mon 26/2/18	Sun 25/2/18			1							
Wall and Floor Tiles 186 BS Installation	10 days	Mon 26/2/18	Wed 7/3/18		1	i.			1				i i
187 Ceiling Installation	10 days 21 days	Thu 8/3/18 Sun 18/3/18	Sat 17/3/18 Sat 7/4/18			1			1				
 Ceiling Installation General Cleaning and Inspection of Mock Up 	21 days 7 days	Sun 8/4/18	Sat 14/4/18		I	i.			i.				
General Cleaning and inspection of Mock op G/F Entrance lobby	44 days	Sun 15/4/18	Mon 28/5/18			l.							
190 Confirmation of Setting Out	7 days	Sun 15/4/18	Sat 21/4/18		i I	1			i i				
191 Flooring screeding	7 days 7 days	Sun 22/4/18	Sat 28/4/18		1	1	i		1				i i
 ¹⁹² Wall and Floor Tiles 	10 days	Sun 29/4/18	Tue 8/5/18			1			I I				
193 BS Installation	10 days	Wed 9/5/18	Fri 18/5/18		i.	i			i.				
194 Ceiling Installation	3 days	Sat 19/5/18	Mon 21/5/18		1	l.			1				
195 General Cleaning and Approval of Mock Up	7 days	Tue 22/5/18	Mon 28/5/18		i I								
¹⁹⁶ Grasscrete (G/F External parking area)	64 days	Tue 15/5/18	Tue 17/7/18		1	1			I.	1			1
197 Surface preparation	28 days	Tue 15/5/18	Mon 11/6/18										
198 Lay sub-base and sand	12 days	Tue 12/6/18	Sat 23/6/18		i.	i			i	i i			i i
199 Lay grasscrete block	12 days	Sun 24/6/18	Thu 5/7/18										
200 Soil and seed	12 days	Fri 6/7/18	Tue 17/7/18										
201 Recycled plastic	72 days	Tue 15/5/18	Wed 25/7/18		1	1			l.				1
202 External cladding & louvre feature	56 days	Tue 15/5/18	Mon 9/7/18										
203 Setting out works	7 days	Tue 15/5/18	Mon 21/5/18		i i	i			i	i i			i i
204 Installation of GMS frame	28 days	Tue 22/5/18	Mon 18/6/18										
205 Fixing of recycle plastic	21 days	Tue 19/6/18	Mon 9/7/18		i I	i i			i				
Green wall feature	56 days	Tue 15/5/18	Mon 9/7/18										
207 Setting out works	7 days	Tue 15/5/18	Mon 21/5/18			1							
208 Installation of GMS frame	28 days	Tue 22/5/18	Mon 18/6/18		1	i	i		1	1			í í
Fixing of recycle plastic	21 days	Tue 19/6/18	Mon 9/7/18			1			1				
Parapet wall feature 211 Setting out works	56 days	Thu 31/5/18	Wed 25/7/18		Í.	i			1	- i			í í
	7 days	Thu 31/5/18	Wed 6/6/18			l.							
	28 days	Thu 7/6/18	Wed 4/7/18		i I				i				
	21 days	Thu 5/7/18	Wed 25/7/18		1	l.			1				i i
214 Major Material Submission and Approval (details	379 days	Thu 23/3/17	Fri 6/4/18			1			I I				
refer to submission schedule) 215 Solid concrete block	0 days	Mop 14/10/17	Mon 16/10/17		I	i.			i.				♦ 16/
	0 days	Mon 16/10/17	Mon 16/10/17			1			1		♦ 11/5		▼ 10/
	0 days	Thu 11/5/17 Mon 3/7/17	Thu 11/5/17 Mon 3/7/17			I						3/7	
Cementitious waterproofing coating 218 Floor Tiles	0 days	Mon 3/7/17	Mon 3/7/17 Eri 20/10/17		1	i			1	- i	•		♦ 2
219 Wall Tiles	0 days 0 days	Fri 20/10/17 Wed 14/6/17	Fri 20/10/17 Wed 14/6/17			1			1		♦ 14/6		V
220 Plastic laminate panel (wood grain pattern)	0 days 0 days	Wed 17/5/17	Wed 17/5/17		i I	1			i		▲ 17/5		
Acoustic timber wall panel system	0 days 90 days	Sun 7/1/18	Fri 6/4/18		1	1			1				1
Folding partitions	90 days 89 days	Sun 7/1/18	Thu 5/4/18			1							
223 Ironmongeries	0 days	Wed 7/6/17	Wed 7/6/17		I.	i			1	i i i	♦ 7/6		i li
224 Toilet cubicle partitions	0 days	Thu 13/7/17	Thu 13/7/17			1						▲ 13/7	
225 Ceiling System	90 days	Sun 7/1/18	Fri 6/4/18		I	1			i.				
226 Locker system	0 days	Thu 13/7/17	Thu 13/7/17		I.	1						▲ 13/7	
Electer system External recycle plastic features	0 days	Tue 20/6/17	Tue 20/6/17			I I					♦ 20/6	ŝ	
Recycle plastic trellis (Type 1)	0 days	Tue 20/6/17	Tue 20/6/17		i.	i			1	- i	♦ 20/6		
Recycle wood plastic composite with aluminium	0 days	Tue 20/6/17	Tue 20/6/17			l.			1		♦ 20/6		
core section wall cladding	5 44/5	. 30 20/0117							i -				
230 Vinyl floor tile	0 days	Thu 23/3/17	Thu 23/3/17		1	i			1	23/3			- i
231 Carpet tile	0 days	Tue 16/1/18	Tue 16/1/18		I.	l.							
	5 44 15	. 30 . 0/ 1/ 10			1	I				1 1 1			
	Critical Path	Progress	Milestone		mary								

7-13 Feb 2016 and 27 Jan- 2 Feb 2017 and 16 Feb - 19 Feb 2018 Chinese New Year site close

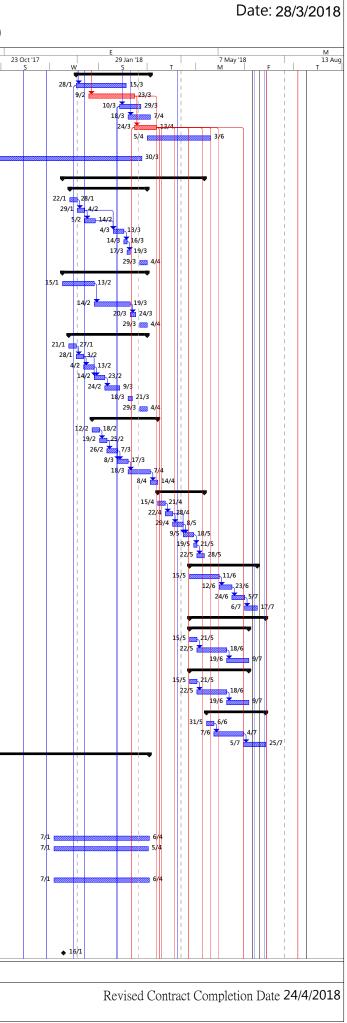


China Road and Bridge Corporation

Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

ID Task Name	Duration	Start	Finish	7 Dec '15 F T	s	14 Mar '16 W	S	20 Jun '16 T M	26 Sep '16 F T	M 2 Jan '17 S W	10 Apr	'17 T	17 Jul '17 M F	7 Т
 External and internal paint Shop drawing Submission and Approval (details 	0 days 147 days	Tue 16/1/18 Sun 4/2/18	Tue 16/1/18 Sat 30/6/18											
refer to submission schedule)					į.									
Glazing doors Metal Door and access papels	60 days	Sun 11/2/18	Wed 11/4/18		i i									
 Metal Door and access panels Recycled Plastic Feature 	60 days 80 days	Sun 11/2/18 Sun 4/2/18	Wed 11/4/18 Tue 24/4/18		l.		1			I.				
 ⁷ Suspensed Ceiling and Fire Resisting Enclosure System 	60 days	Sun 11/2/18	Wed 11/4/18											
Fall Arrest System	30 days	Sun 18/2/18	Mon 19/3/18		Ì		i i							
Acoustic Timber Wall Panel System Acoustic Operable Wall System	60 days 60 days	Sun 11/2/18 Sun 25/2/18	Wed 11/4/18 Wed 25/4/18		i.									
Acoustic Operable Wall System Timber Door	60 days	Sun 18/2/18	Wed 25/4/18 Wed 18/4/18		i.		1			I I				
42 Timber Cabinet	60 days	Sun 11/2/18	Wed 11/4/18		I I		1							
Roller Shutters and Fire Shutters Metal railing system	60 days	Sun 18/2/18	Wed 18/4/18		1									
 Metal railing system Waterproofing System 	60 days 60 days	Sun 11/2/18 Sun 4/2/18	Wed 11/4/18 Wed 4/4/18		į.		i i							
Toilet and Shower Cubicle Partition Systems	60 days	Sun 11/2/18	Wed 11/4/18		i i		1							
47 Changing Room Lockers System	60 days	Sun 25/2/18	Wed 25/4/18		I.		i i							
Signage Internal Finishing Works	60 days	Wed 2/5/18	Sat 30/6/18		I I		1							
49 Internal Finishing Works 50 Block Wall Erection	292 days 211 days	Wed 1/11/17 Thu 7/12/17	Sun 19/8/18 Thu 5/7/18		j.		i i							
51 G/F	60 days	Thu 7/12/17	Sun 4/2/18		i.		1			I I				i i
⁵² UG/F	90 days	Sun 14/1/18	Fri 13/4/18	I I	l L		1			l I				
53 1/F 54 2/F	60 days	Sun 4/2/18 Sun 11/3/18	Wed 4/4/18 Wed 9/5/18		I.		1							
55 3/F	60 days 60 days	Mon 16/4/18	Thu 14/6/18	i i	l l		1							
56 4/F	60 days	Mon 7/5/18	Thu 5/7/18	1	l.		1							
57 Window and Louver 58 Internal Waterproofing works	80 days	Mon 21/5/18	Wed 8/8/18		l I		1			1				
 Internal Waterproofing works Plastering, Tiling & Laying Floor Screed 	120 days 260 days	Mon 26/2/18 Wed 1/11/17	Mon 25/6/18 Wed 18/7/18	1	l.		i i			1				1/11
Carpentry & Joinery/ Ironmongery and Door	70 days	Wed 30/5/18	Tue 7/8/18		l l									
Installation				1	l.		1			i I				
Metal Works (Roller Shutter, railing) False Ceiling	90 days	Sun 22/4/18 Wed 30/5/18	Fri 20/7/18 Sat 28/7/18		l I		1			l I				
 False Ceiling Flooring Finishes 	60 days 50 days	Wed 30/5/18 Fri 29/6/18	Sat 28/7/18 Fri 17/8/18		i.									
⁵⁴ Painting	92 days	Sun 20/5/18	Sun 19/8/18		i.									
55 Internal painting (Final Coat) 56 G/F	92 days	Sun 20/5/18	Sun 19/8/18		L L		1							
66 G/F 57 UG/F	28 days 28 days	Sun 20/5/18 Sun 3/6/18	Sat 16/6/18 Sat 30/6/18		1									1
⁵⁸ 1/F	28 days	Sat 16/6/18	Fri 13/7/18		Ì		i i							
69 2/F	28 days	Fri 29/6/18	Thu 26/7/18		į.									
70 3/F 71 4/F	21 days	Thu 12/7/18 Wed 18/7/18	Wed 1/8/18 Tue 7/8/18		1		1							
72 R/F	21 days 21 days	Tue 24/7/18	Mon 13/8/18		1		1							1
73 UR/F	21 days	Mon 30/7/18	Sun 19/8/18		j.									
External Wall Preparation Works for Curtain Wall Installation CW1, CW2 External Wall Preparation Works for Curtain Wall	30 days	Sat 14/4/18	Sun 13/5/18											
275 External Wall Preparation Works for Curtain Wall Installation CW3, CW4, CW5, CW6	23 days	Sun 6/5/18	Mon 28/5/18											
76 External Wall Plastering and Tiling Works 77 External painting	45 days	Sat 14/4/18	Mon 28/5/18		l.		1							
77 External painting 78 Roofing works	30 days 80 days	Tue 29/5/18 Tue 1/5/18	Wed 27/6/18 Thu 19/7/18		į.		i i							
79 Waterproofing Application	45 days	Tue 1/5/18	Thu 14/6/18		į.									
80 Waterproofing Testing	14 days	Fri 15/6/18	Thu 28/6/18		I I		1			1				
⁸¹ Roof tiling ⁸² Sanitary fittings installation	21 days 41 days	Fri 29/6/18 Fri 1/6/18	Thu 19/7/18 Wed 11/7/18		I I									
⁸³ G/F ~ 1/F	14 days	Fri 1/6/18	Thu 14/6/18		i.									
84 2/F ~ 4/F	20 days	Fri 15/6/18	Wed 4/7/18		i i									
R/F ~ UR/F B Submission of Aluminium window/ louvre &	7 days 289 days	Thu 5/7/18 Sat 30/9/17	Wed 11/7/18 Sun 15/7/18											
Curtain Wall Submission	193 days	Sat 30/9/17	Tue 10/4/18		i i		I I							
88 CW1~CW6 Shop Drg. & Calculation	1 day	Sat 30/9/17	Sat 30/9/17		l l		1						E	30/9 30/9
(re-submission) 9 Review & Approval by P&T	16 days	Sun 1/10/17	Mon 16/10/17		I I		1			l I				1/10 16/10
Visual Mock-up Drg. (CW3)	1 day	Thu 19/10/17	Thu 19/10/17				1			1				19/10 19/1
Control Mock-up Drg. (CW3)	1 day	Thu 19/10/17	Thu 19/10/17		į.		i i							19/10 19/10
Review & Approval by P&T Performance Test Drg. (CW1) and Test Proposa	30 days	Fri 20/10/17 Fri 27/10/17	Sat 18/11/17 Eri 27/10/17		l I		1							20/10 27/10 527
Performance Test Drg. (CW1) and Test Propose Review & Approval by P&T	1 day 30 days	Sat 28/10/17	Fri 27/10/17 Sun 26/11/17		I I		1	l		l I				28/10
95 Glass Sample	1 day	Fri 17/11/17	Fri 17/11/17		1		1							17,
Window Hardware Glass & Hardware Review & Approval by P&T	1 day	Fri 24/11/17	Fri 24/11/17		Ì									18
 Glass & Hardware Review & Approval by P&T PVDF Color Guide 	14 days 7 days	Sat 18/11/17 Sun 19/11/17	Fri 1/12/17 Sat 25/11/17		l.		1							18
9 Review & Color Selected by P&T	28 days	Wed 14/3/18	Tue 10/4/18		I I		1			l I				
⁰⁰ Visual Mock-up (Off Site)	176 days	Tue 17/10/17	Tue 10/4/18		I.		1			1				17/10
Ordering, Die Making & Extrusion of Aluminium material	60 days	Tue 17/10/17	Fri 15/12/17				1							17/10
PVDF coating Ordering and Exprication of GMS bracket/frame	3 days	Sat 16/12/17	Mon 18/12/17		I I		1	l						
 Ordering and Fabrication of GMS bracket/frame Fabrication of Aluminium Frames 	14 days 45 days	Sun 24/12/17 Sun 31/12/17	Sat 6/1/18 Tue 13/2/18	1	1		1			1				
⁰⁵ Glass Production	45 days 45 days	Sun 7/1/18	Tue 13/2/18		į.					1				
D6 Erection of Temproary Steel frame	14 days	Sun 4/2/18	Sat 17/2/18		l l		1							
Erection of Aluminium Frames Glazing Works	9 days	Sun 18/2/18	Mon 26/2/18	1	I I		1			l I				
D8 Glazing Works	3 days	Fri 9/3/18	Sun 11/3/18		1					1				
	ritical Path	Progress		 Milestone Su 	mmary 🛡									

7-13 Feb 2016 and 27 Jan- 2 Feb 2017 and 16 Feb - 19 Feb 2018 Chinese New Year site close

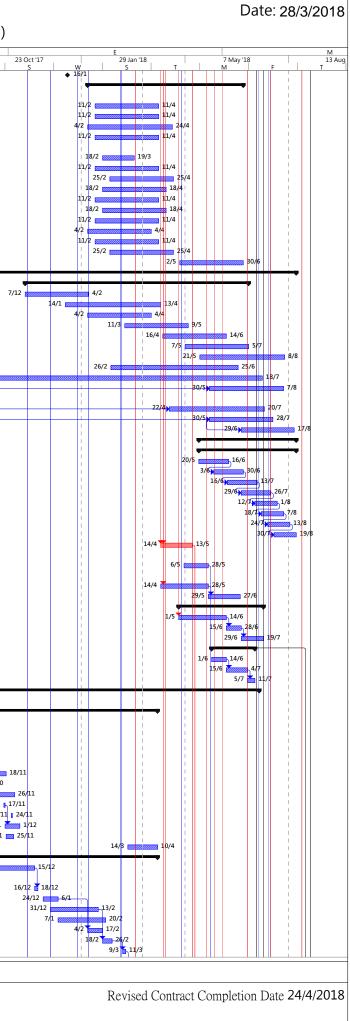


Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

	Fask Name	Duration	Start	Finish
	Inspection & Approval of Mock-up	28 days	Wed 14/3/18	Tue 10/4/18
	ontrol Mock-up(CW3 - on site) Ordering, Die Making & Extrusion of Aluminium	94 days 33 days	Sun 4/2/18 Sun 4/2/18	Tue 8/5/18 Thu 8/3/18
	terial	55 uays	3un 4/2/10	1110 0/3/10
	PVDF coating	8 days	Fri 9/3/18	Fri 16/3/18
	Ordering and Fabrication of GMS bracket/frame Fabrication of Aluminium Frames	14 days 14 days	Mon 12/3/18 Sat 17/3/18	Sun 25/3/18 Fri 30/3/18
	Glass Production	18 days	Wed 11/4/18	Sat 28/4/18
	Erection of Temproary Steel frame	14 days	Wed 11/4/18	Tue 24/4/18
	Erection of Aluminium Frames	18 days	Mon 16/4/18	Thu 3/5/18
	Glazing Works Inspection of Mock-up	4 days	Fri 4/5/18 Tue 8/5/18	Mon 7/5/18 Tue 8/5/18
	Performance Test Mock-up (CW1 - HK	1 day 87 days	Sun 14/1/18	Tue 10/4/18
	Laboratory)	o, aajo	our rivin to	
	Ordering, Die Making & Extrusion of Aluminium	35 days	Sun 14/1/18	Sat 17/2/18
	material PVDF coating	3 days	Mon 29/1/18	Wed 31/1/18
	Ordering and Fabrication of GMS bracket/frame	16 days	Sun 4/2/18	Mon 19/2/18
	Fabrication of Aluminium Frames	25 days	Sun 4/2/18	Wed 28/2/18
	Glass Production	30 days	Sun 11/2/18	Mon 12/3/18
	Erection of Temproary Steel frame	21 days	Sun 25/2/18	Sat 17/3/18
	Erection of Aluminium Frames Glazing Works	18 days 5 days	Sun 11/3/18 Thu 29/3/18	Wed 28/3/18 Mon 2/4/18
	Pre-testing	3 days	Tue 3/4/18	Thu 5/4/18
	Official Preformance Test	2 days	Mon 9/4/18	Tue 10/4/18
	Permanent Works	126 days	Mon 12/3/18	Sun 15/7/18
	Ordering & Die Making	14 days	Mon 12/3/18	Sun 25/3/18
ŀ	Extrusion of Aluminium material PVDF coating	8 days 3 days	Mon 26/3/18 Tue 3/4/18	Mon 2/4/18 Thu 5/4/18
	Ordering and Fabrication of GMS bracket/frame	25 days	Mon 19/3/18	Thu 12/4/18
	Ordering & Production of Window hardware	30 days	Mon 26/3/18	Tue 24/4/18
	Fabrication of Aluminium Frames	30 days	Mon 2/4/18	Tue 1/5/18
	Glass Production	46 days	Mon 9/4/18	Thu 24/5/18
+	Inspection of Heat soak test Delivery & Erection of Steel frame	7 days 30 days	Fri 25/5/18 Mon 23/4/18	Thu 31/5/18 Tue 22/5/18
	Delivery & Hositing of Aluminium Frames	23 days	Mon 30/4/18	Tue 22/5/18
1	Erection of Aluminium Frames (CW1, CW2)	31 days	Mon 14/5/18	Wed 13/6/18
	Erection of Aluminium Frames (CW3, CW4,	32 days	Tue 29/5/18	Fri 29/6/18
-	CW5, CW6) Delivery & Hositing of Glass panels	30 days	Fri 1/6/18	Sat 30/6/18
t	Glazing works	21 days	Thu 14/6/18	Wed 4/7/18
	Field watertighness test	7 days	Thu 5/7/18	Wed 11/7/18
1	Protection	4 days	Thu 12/7/18	Sun 15/7/18
	External and Landscaping works	92 days	Sun 13/5/18	Sun 12/8/18
+	Recycled Products Installation Roads and pavings	40 days 30 days	Mon 21/5/18 Sun 17/6/18	Fri 29/6/18 Mon 16/7/18
	Removal of scaffoldings	28 days	Thu 5/7/18	Wed 1/8/18
	Hard Landscaping	51 days	Mon 4/6/18	Tue 24/7/18
	R.C. Planter	45 days	Mon 4/6/18	Wed 18/7/18
	Movable planter	45 days	Mon 4/6/18	Wed 18/7/18
-	Trellises Benches	45 days 30 days	Mon 4/6/18 Mon 25/6/18	Wed 18/7/18 Tue 24/7/18
╉	Soft Landscaping	30 days 92 days	Sun 13/5/18	Sun 12/8/18
1	Soft Landscaping - Material Submission/	28 days	Sun 13/5/18	Sat 9/6/18
	Preparation works			
L	Soft Landscaping - Filing of soil	21 days	Mon 18/6/18	Sun 8/7/18
	Soft Landscaping - Plant Delivery	7 days	Mon 9/7/18	Sun 15/7/18
	Soft Landscaping - Planting works (Plus 12-months Establishment Period)	28 days	Mon 16/7/18	Sun 12/8/18
	Site enclosure and divisions	80 days	Mon 14/5/18	Wed 1/8/18
	Construction of fence wall	60 days	Mon 14/5/18	Thu 12/7/18
	Installation of metal gates	20 days	Fri 13/7/18	Wed 1/8/18
	Builder's works for external services	60 days	Mon 4/6/18 Mon 1/8/16	Thu 2/8/18 Wed 18/7/18
	umbing Services (see also detail programme r Plumbing trade)	717 days		weu 18///18
	Drawing Submission and Approval (details refer	400 days	Mon 1/8/16	Mon 4/9/17
	to submission schedule)			
	Equipment & Material submission Approval	170 days	Sun 6/11/16	Mon 24/4/17
+	(details refer to submission schedule) Submission / Application of Form WWO 046 (Part	6 days	Fri 17/3/17	Wed 22/3/17
	I & II)	o udys	FILT/3/17	weu 22/3/17
t	G/F to R/F Plumbing Installation	158 days	Sun 4/2/18	Wed 11/7/18
	G/F Plumbing Installation	60 days	Sun 4/2/18	Wed 4/4/18
+	UG Plumbing Installation	65 days	Mon 12/3/18	Tue 15/5/18
+	1/F Plumbing Installation 2/F Plumbing Installation	60 days 60 days	Sun 18/3/18 Sun 8/4/18	Wed 16/5/18 Wed 6/6/18
	3/F Plumbing Installation	60 days	Sun 22/4/18	Wed 20/6/18
l	4/F Plumbing Installation	60 days	Sun 6/5/18	Wed 4/7/18
	R/F Plumbing Installation	45 days	Sun 27/5/18	Tue 10/7/18
	Submission of Form WWO 046 (Part IV)	1 day	Wed 11/7/18	Wed 11/7/18
	Handover of All Water Tank & Pump Rooms at UG Handover of All Water Tank & Pump Rooms at 2/F	1 day 1 day	Thu 15/3/18 Mon 30/4/18	Thu 15/3/18 Mon 30/4/18
t	Testing & Commissioning	30 days	Mon 11/6/18	Tue 10/7/18
1	WSD Inspection	5 days	Thu 12/7/18	Mon 16/7/18
	Anticipated Receipt of Form WWO 046 (Part V)	1 day	Tue 17/7/18	Tue 17/7/18
	D505 - Master Construction Task			

7-13 Feb 2016 and 27 Jan- 2 Feb 2017 and 16 Feb - 19 Feb 2018 Chinese New Year site close

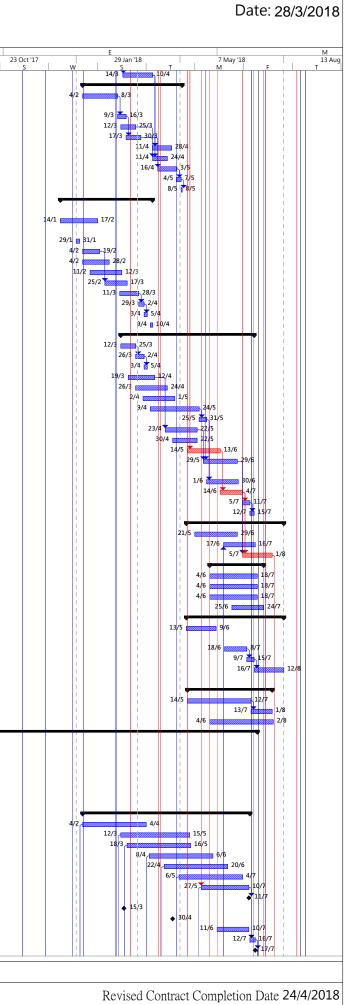


China Road and Bridge Corporation

Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

ID Task Name	Duration	Start	Finish	B 7 Dec '15 F T S	14 Mar '16 5 W S	E 20 Jun '16	26 Sep '16 F T	M 2 Jan '17 S W	10 Apr '17 S T	B 17 Jul '1' M F	7 7 T
384 Obtain Water Certificate 385 Drainage Services (see also detail programme	1 day 742 days	Wed 18/7/18 Mon 1/8/16	Wed 18/7/18 Sun 12/8/18							_	
for Drainage trade)						1/8	28/11				1
⁸⁶ Drawing Submission and Approval (details refer to submission schedule)	120 days	Mon 1/8/16	Mon 28/11/16		1			I I			
¹⁸⁷ Equipment & Material submission Approval	120 days	Sun 6/11/16	Sun 5/3/17				6/11	5/3			
(details refer to submission schedule) 88 Aboveground G/F to UR Drainage Installation	151 days	Mon 12/3/18	Thu 9/8/18								
⁸⁹ G/F Drainage Installation	60 days	Mon 12/3/18	Thu 10/5/18								
90 UG Drainage Installation 91 1/F Drainage Installation	60 days	Mon 9/4/18 Mon 14/5/18	Thu 7/6/18 Wed 27/6/18								
392 2/F Drainage Installation	45 days 45 days	Mon 28/5/18	Wed 11/7/18								
393 3/F Drainage Installation	45 days	Mon 4/6/18	Wed 18/7/18		1	1		1			
4/F Drainage Installation R/F Drainage Installation	45 days 15 days	Mon 11/6/18 Mon 9/7/18	Wed 25/7/18 Mon 23/7/18					I I			I I
VF Drainage installation UR Drainage Installation	15 days	Tue 24/7/18	Tue 7/8/18		1						
397 Testing & Commissioning	60 days	Mon 11/6/18	Thu 9/8/18					i i			
98 Underground Drainage 99 Inside Building Installation	463 days 180 days	Sun 7/5/17 Mon 20/11/17	Sun 12/8/18 Fri 18/5/18								20/11
⁰⁰ Inside Building Drain Test	180 days	Mon 25/12/17	Fri 22/6/18		1			I I			
01 Outside Building Installation (within site boundar 02 Outside Building Drain Test (within site boundar	90 days	Mon 14/5/18	Sat 11/8/18		1			I I			
 Outside Building Drain Test (within site boundar Excavation Permit Application 	90 days 80 days	Tue 15/5/18 Mon 10/7/17	Sun 12/8/18 Wed 27/9/17					I I	10/	7	27/9
⁰⁴ Preparation of Form HBP1	1 day	Sun 7/5/17	Sun 7/5/17						7/5 7/5		
⁴⁰⁵ Submission of Form HBP1	21 days	Mon 8/5/17	Sun 28/5/17						8/5 28/5		
IO6 Construction of Terminal Manholes IO7 Final Connection to Government Manhole	120 days	Wed 1/11/17 Mon 5/3/18	Wed 28/2/18 Mon 30/4/18								1/11
 ⁰⁸ Final Drainage Submission 	57 days 30 days	Mon 5/3/18 Mon 16/4/18	Tue 15/5/18		l l		1	I 			
109 DSD Inspection	60 days	Mon 30/4/18	Thu 28/6/18			1		 			
¹⁰ Electrical installations (see also detail programme for EL trade)	928 days	Mon 1/2/16	Thu 16/8/18							_	
Drawing Submisssion and Approval (details refer	300 days	Sat 2/7/16	Thu 27/4/17			2/7			27/4		
to submission schedule) H2 Equipment & Material Submisssion and Approval	300 days	Sat 2/7/16	Thu 27/4/17		1	2/7		1	27/4		
(details refer to submission schedule)	500 days										
Conceal conduit & Builder work for Electrical / ELV System	190 days	Fri 6/10/17	Fri 13/4/18								6/10
ELV System ¹⁴ G/F (G.L.1-5/A-K)	45 days	Sun 8/10/17	Tue 21/11/17								8/10
¹¹⁵ G/F (G.L.5-9/A-K)	45 days	Sun 15/10/17	Tue 28/11/17					I I			15/10
¹¹⁶ UG/F (G.L.1-5/A-K) ¹¹⁷ UG/F (G.L.5-9/A-K)	45 days	Sun 22/10/17	Tue 5/12/17					I I			22/10 29/10
¹¹⁷ UG/F (G.L.5-9/A-K) ¹¹⁸ 1/F (G.L.1-5/A-K)	45 days 45 days	Sun 29/10/17 Sun 26/11/17	Tue 12/12/17 Tue 9/1/18		1						26/11
¹¹⁹ 1/F (G.L.5-9/A-K)	45 days	Sun 20/11/17 Sun 17/12/17	Tue 30/1/18								
⁴²⁰ 2/F (G.L.1-5/A-K)	45 days	Sun 31/12/17	Tue 13/2/18			I I		I I			
⁴²¹ 2/F (G.L.5-9/A-K) ⁴²² 3/F (G.L.1-5/A-K)	45 days 30 days	Sun 14/1/18 Sun 4/2/18	Tue 27/2/18 Mon 5/3/18					I I I			
⁴²³ 3/F (G.L.5-9/A-K)	30 days	Sun 18/2/18	Mon 19/3/18					I I I			
⁴²⁴ 4/F (G.L.1-5/A-K)	15 days	Sun 18/3/18	Sun 1/4/18	i i				i i			
⁴²⁵ 4/F (G.L.5-9/A-K) ⁴²⁶ R/F (G.L.1-5/A-K)	15 days 8 days	Sun 25/3/18 Sat 14/4/18	Sun 8/4/18 Sat 21/4/18								
⁴²⁷ R/F (G.L.5-9/A-K)	8 days	Sun 22/4/18	Sun 29/4/18					I I			
G/F to R/F Electrical Installation - First fixing	277 days	Wed 18/10/17	Sat 21/7/18		1			I I I			
¹²⁹ G/F Electrical installation	50 days	Mon 14/5/18	Mon 2/7/18					1			
430 UG Electrical installation 431 1/F Electrical Installation	60 days 60 days	Mon 19/3/18 Mon 26/3/18	Thu 17/5/18 Thu 24/5/18			i i		i i			
132 2/F Electrical installation	60 days	Mon 2/4/18	Thu 31/5/18								
 33 3/F Electrical Installation 44/F Electrical Installation 	60 days	Mon 16/4/18	Thu 14/6/18		l l			1 			
4/F Electrical Installation R/F Electrical Installation	60 days 60 days	Mon 30/4/18 Mon 14/5/18	Thu 28/6/18 Thu 12/7/18			1		 			
¹³⁶ Completion of CLP G/F Tx. Room	1 day	Wed 18/10/17	Wed 18/10/17								18/10 18/10
¹³⁷ Installation Work of E&M Services & builder's	59 days	Thu 19/10/17	Sat 16/12/17								19/10
works inside Tx. Room Handover G/F Tx. Room for CLP Installation	17 days	Sun 17/12/17	Tue 2/1/18								
Work											
439 CLP Installation Work in Tx. Room 440 CLP Inspection & Power Energisation	120 days 9 days	Wed 3/1/18 Fri 13/7/18	Wed 2/5/18 Sat 21/7/18					I			
440 CLP Inspection & Power Energisation 441 Electrical final fix (Lighting Fittings / Wiring	9 days 50 days	Mon 30/4/18	Sat 21/1/18 Mon 18/6/18		1	I I		 			
Accessories / ELV Accessories)											
142 G/F 143 LIG/E	75 days	Mon 23/4/18	Fri 6/7/18								
443 UG/F 444 1/F	60 days 60 days	Mon 2/4/18 Mon 23/4/18	Thu 31/5/18 Thu 21/6/18		1	i I	1				
145 2/F	60 days	Mon 30/4/18	Thu 28/6/18			l I		I I I I			
446 3/F	60 days	Mon 7/5/18	Thu 5/7/18								
147 4/F 148 R/F	60 days 60 days	Mon 14/5/18 Mon 14/5/18	Thu 12/7/18 Thu 12/7/18								
Hand Hand Hand Hand Hand Hand Hand Hand	280 days	Mon 2/10/17	Sun 8/7/18								2/10
Testing & Commissioning (Electrical Installation)	22 days	Wed 18/7/18	Wed 8/8/18					I I			
 T&C for Earthing & Lightning System T&C for Menger Test of Power Cable & Wiring 	45 days	Mon 18/6/18	Wed 1/8/18								
 T&C for Megger Test of Power Cable & Wiring T&C for Distribution Board 	45 days 45 days	Mon 18/6/18 Mon 18/6/18	Wed 1/8/18 Wed 1/8/18								
⁵⁴ T&C for Power Management System	45 days	Mon 18/6/18	Wed 1/8/18		1						
55 T&C for Lighting Fitting & Small Power	60 days	Mon 4/6/18	Thu 2/8/18			l l		I I			
456 T&C for PV System 457 LVSB System	45 days	Mon 18/6/18	Wed 1/8/18			1					<u>!</u>
457 LVSB. System	787 days	Fri 15/4/16	Sun 10/6/18		· · · · · · · · · · · · · · · · · · ·						
roject: SSD505 - Master Construction Task	Critical Path	Progress		Milestone	20/						
te: Wed 28/3/18	Citucar Path	Progress		winestone	ary —						
Remarks: *Delay in selection of nile for lo	P		1 1949				Page 6				

Remarks: *Delay in selection of pile for loading test and Special ground conditions subject to EOT claim 7-13 Feb 2016 and 27 Jan- 2 Feb 2017 and 16 Feb - 19 Feb 2018 Chinese New Year site close

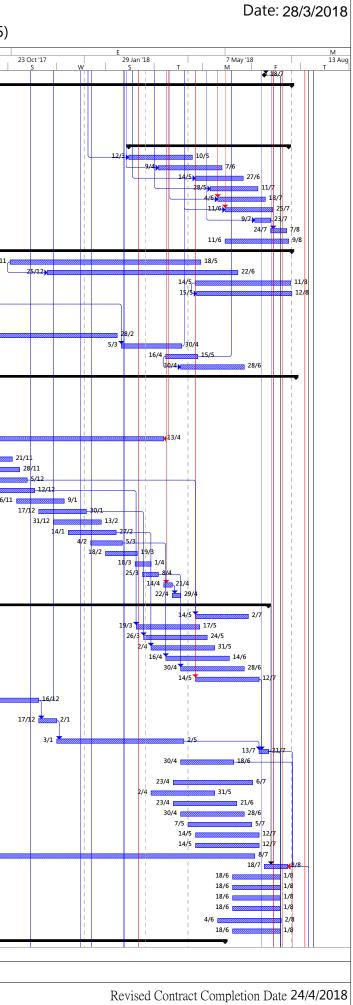

China Road and Bridge Corporation

Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

26 Sep '16 F

22/10

1/10

14/12

14/1

M

31/8

M 2 Jan '17 S W

31/1

10 Apr '17

S

17/4

B 17 Jul '17

17/


9/10

22/0

ID	Task Name	Duration	Start	Finish	В	7 Dec '15	14 Mar '16	E 20 Jun '16
458	Drawing Submisssion and Approval of LVSB	111 days	Fri 13/5/16	Wed 31/8/16	F	T S	W 13/5	S T
159	(details refer to submission schedule)			Fri 15/7/16			15/4	15/7
	Equipment & Material Submisssion and Approval of LVSB (details refer to submission	92 days	Fri 15/4/16	FII 15/7/10			25/4	1
60	Handover LV Switch Room for Elect / LV Sw.Bo	31 days	Tue 5/12/17	Thu 4/1/18	1			i i
61 62	E&M Work inside LV Switch Room	90 days	Fri 5/1/18	Wed 4/4/18				
+62 463	LV Cubicle Switchboard Installation Site Test for LV Switchboard	40 days 20 days	Mon 12/3/18 Mon 19/3/18	Fri 20/4/18 Sat 7/4/18	1			
464	Handover 1/F-4/F Sub-S.W. Rm. For Electrical	64 days	Sun 8/4/18	Sun 10/6/18	1			
	Work	0 r ddy5	Sundrinto	341110/0/10				
65	Generator	905 days	Mon 1/2/16	Tue 24/7/18		-		
166	Drawing Submisssion and Approval of	140 days	Thu 14/4/16	Wed 31/8/16			14/4	
167	Generator (details refer to submission Equipment & Material Submission and	151 days	Mon 1/2/16	Thu 30/6/16	1	1/2		30/6
	Approval of Generator (details refer to submission schedule)	151 0495	WUT 1/2/16	1110 30/0/10				
168	Submission Application for EPD (Generator Set System)	62 days	Mon 22/8/16	Sat 22/10/16				22/8 📷
169	Handover 3/F & R/F Generator Room for Installation Work	45 days	Mon 7/5/18	Wed 20/6/18				
470	Diesel Generator Installation	60 days	Mon 7/5/18	Thu 5/7/18				
71	Site Test for Diesel Generator Installation	19 days	Fri 6/7/18	Tue 24/7/18				
72	ELV. System	611 days	Wed 14/12/16	Thu 16/8/18	1			1
73	Drawing Submisssion and Approval of ELV (details refer to submission schedule)	49 days	Wed 14/12/16	Tue 31/1/17				
474	Broadcast Reception Installation	80 days	Mon 7/5/18	Wed 25/7/18				
475 476	Burglar Alarm and Security Installation	80 days	Mon 21/5/18	Wed 8/8/18				
77	Audio Electronic Installation T&C for CABD System	80 days 60 days	Mon 28/5/18 Mon 18/6/18	Wed 15/8/18 Thu 16/8/18				
178	T&C for CCTV System	60 days	Mon 18/6/18	Thu 16/8/18 Thu 16/8/18	1			1
179	T&C for PA System	60 days	Mon 18/6/18	Thu 16/8/18				
80	T&C for Watchman Tour System	60 days	Mon 18/6/18	Thu 16/8/18				
81	T&C for Smart Card System	60 days	Mon 18/6/18	Thu 16/8/18	1			
182 183	T&C for Induction Loop	60 days	Mon 18/6/18	Thu 16/8/18				
33 34	T&C for energy management system Mechanical Ventilation and Air conditioning	60 days 930 days	Mon 18/6/18 Fri 5/2/16	Thu 16/8/18 Wed 22/8/18				L
	installations (see also detail programme for MVAC trade)	930 UAYS	F11 3/2/10	weu 22/0/10		•		
5	Drawing Submisssion and Approval (details refer to submission schedule)	240 days	Sat 14/1/17	Sun 10/9/17				
86	Equipment & Material Submisssion and Approval (details refer to submission schedule)	240 days	Fri 5/2/16	Sat 1/10/16		5/2		
87	Major MVAC Material Delivery	179 days	Sun 10/12/17	Wed 6/6/18				
88	Cooling Tower	120 days	Sun 10/12/17	Sun 8/4/18				
89 90	Water Cooled Chiller	120 days	Sun 17/12/17	Sun 15/4/18				
91	Water Scrubber Heat Pump Unit	120 days 120 days	Sun 31/12/17 Mon 5/2/18	Sun 29/4/18 Mon 4/6/18				
92	Heat Transfer Compact Unit	120 days	Mon 5/2/18	Mon 4/6/18	1			
193	Water Calorifier	120 days	Mon 5/2/18	Mon 4/6/18				
94	Water Pump	120 days	Wed 7/2/18	Wed 6/6/18	i	i		i
195	MCC	100 days	Sun 31/12/17	Mon 9/4/18				
196 197	Flat Plat type Solar Collector Vehicle Exhaust Extraction System	100 days 100 days	Tue 27/2/18	Wed 6/6/18 Sat 21/4/18	1			
198	Welding Exhaust System	100 days	Fri 12/1/18 Fri 12/1/18	Sat 21/4/18	1			
199	Automatic Condenser Tube Cleaning System	100 days	Sun 7/1/18	Mon 16/4/18				
500	Submission & Approval of AC Layout(Initial) by WS	22 days	Sun 17/9/17	Mon 9/10/17				
501	Submission/Application of form WWO 046(Part I	75 days	Mon 9/10/17	Fri 22/12/17	1			
0.2	& II) for Cooling Tower Installation							į
02	Submission of form WWO 046(Part IV) for Cooling Tower Installation	1 day	Wed 13/6/18	Wed 13/6/18				
03	Submission of CT1B & CT4 to EMSD for Cooling Tower Installation	1 day	Fri 22/9/17	Fri 22/9/17				
604	Submission of CT2B to EMSD for Cooling Tower Installation	1 day	Sun 13/5/18	Sun 13/5/18				
505 506	Submission of VAC Drawing(Initial) to FSD Final Submission of VAC form 501 for MVAC Installation	47 days 1 day	Thu 2/3/17 Tue 30/1/18	Mon 17/4/17 Tue 30/1/18				
507	Conceal Conduit & Builder Work for MVAC	180 days	Sun 1/10/17	Thu 29/3/18				
508	G/F to R/F MVAC Installation	158 days	Fri 9/2/18	Mon 16/7/18				
09	G/F MVAC Installation	60 days	Mon 23/4/18	Thu 21/6/18				
10	UG/F MVAC Installation	120 days	Sat 10/2/18	Sat 9/6/18	1	l		
511	Handover of UG/F Chiller Plant for MVAC Installation	1 day	Fri 9/2/18	Fri 9/2/18				
512 513	- UG/F MVAC Installation in Chiller Plant	120 days	Sat 10/2/18	Sat 9/6/18				1
513	Handover of UG/F AHU Rm for MVAC Installatic - UG/F MVAC Installation in AHU Rm	1 day 90 days	Fri 9/2/18 Sat 10/2/18	Fri 9/2/18 Thu 10/5/18				
15	Handover of UG/F Water Pump Rm. for MVAC	90 days 1 day	Tue 6/3/18	Tue 6/3/18				
516	Installation	80 dave	Wod 7/2/10	Eri 25/5/10	1	1		
16	- UG/F MVAC Installation in Water Pump Rm. Handover of UG/F Exhaust Air Fan Rm. for	80 days 1 day	Wed 7/3/18 Mon 16/4/18	Fri 25/5/18 Mon 16/4/18				
	MVAC Installation	i uay	1011 10/4/10	10/11/10/4/10	1			
518	- UG/F MVAC Installation in Exhaust Air Fan Rn	60 days	Tue 17/4/18	Fri 15/6/18				
519	Handover of UG/F MCC Rm. for MVAC	1 day	Tue 6/3/18	Tue 6/3/18	1			1
20	Installation				i			
520	 UG/F MVAC Installation in MCC Rm. 	52 days	Wed 7/3/18	Fri 27/4/18	1	1		1

Remarks: *Delay in selection of pile for loading test and Special ground conditions subject to EOT claim 7-13 Feb 2016 and 27 Jan- 2 Feb 2017 and 16 Feb - 19 Feb 2018 Chinese New Year site close

Page 7

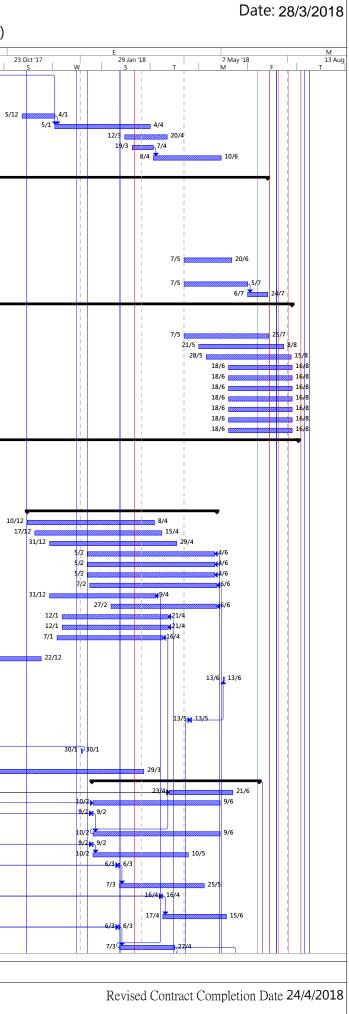


Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

	ask Name	Duration	Start	Finish	
1	Handover of G/F Vehicle Washing Bay for	1 day	Mon 16/4/18	Mon 16/4/1	F 18
	MVAC Installation	(0.1	T 47/4/40	E 1 4 5 1/ 14	
	- G/F MVAC Installation in Vehicle Washing Bay	60 days	Tue 17/4/18	Fri 15/6/1	
	1/F MVAC Installation 2/F MVAC Installation	51 days 51 days	Mon 16/4/18 Mon 30/4/18	Tue 5/6/1 Tue 19/6/1	_
	3/F MVAC Installation	41 days	Mon 28/5/18	Sat 7/7/1	
	Handover of 3/F PAU Rm (West Wing) for	1 day	Tue 24/4/18	Tue 24/4/1	
	MVAC Installation				_
	- 3/F MVAC Installation in PAU Rm (West Wing)	60 days	Wed 25/4/18	Sat 23/6/1	_
	Handover of 3/F PAU Rm (East Wing) for MVAC Installation	1 day	Tue 24/4/18	Tue 24/4/1	18
+	- 3/F MVAC Installation in PAU Rm (East Wing)	60 days	Wed 25/4/18	Sat 23/6/1	18
)	4/F MVAC Installation	35 days	Tue 24/4/18	Mon 28/5/1	_
	Handover of 4/F Cooling Tower Plant for MVAC	1 day	Wed 16/5/18	Wed 16/5/1	
	Installation				_
2	- 4/F MVAC Installation in Cooling Tower Plant	26 days	Thu 17/5/18	Mon 11/6/1	_
3	Handover of PAU Rm (West Wing) for MVAC	1 day	Thu 10/5/18	Thu 10/5/1	18
	Installation - 4/F MVAC Installation in PAU Rm (West Wing)	60 days	Fri 11/5/18	Mon 9/7/1	18
	R/F MVAC Installation	43 days	Mon 4/6/18	Mon 16/7/1	
5	Handover of R/F Heat Pump Plant for MVAC	1 day	Thu 31/5/18	Thu 31/5/1	
	Installation				_
	 R/F MVAC Installation in Heat Pump Plant 	21 days	Fri 1/6/18	Thu 21/6/1	
5	Handover of Flat Roof for MVAC Installation	1 day	Thu 31/5/18	Thu 31/5/1	
,)	- R/F MVAC Installation in Flat Roof	36 days	Fri 1/6/18	Fri 6/7/1	
1	Testing & Commissioning (MVAC) Testing & Commissioning & Handover(MVAC)	20 days 239 days	Fri 20/7/18 Wed 27/12/17	Wed 8/8/1 Wed 22/8/1	
2	Cooling Tower Function & Full Load Test	45 days	Tue 12/6/18	Thu 26/7/1	
3	Water Cooled Chiller Function & Full Load Test	45 days	Fri 15/6/18	Sun 29/7/1	
4	Water Pump Performance Test	45 days	Tue 5/6/18	Thu 19/7/1	
5	Water Pump Alignment Test	45 days	Tue 29/5/18	Thu 12/7/1	
6 7	Water Scrubber Performance Test	45 days	Mon 18/6/18	Wed 1/8/1	
8	Heat Pump Unit Performance Test	30 days	Sat 7/7/18	Sun 5/8/1	
.9	Heat Transfer Compact Unit Performance Test Solar Hot Water System Performance Test	30 days 30 days	Fri 22/6/18 Sat 7/7/18	Sat 21/7/1 Sun 5/8/1	
0	Fan Coil Units Function Test	30 days	Tue 12/6/18	Wed 11/7/1	
1	Water Balancing	30 days	Tue 5/6/18	Wed 4/7/1	
2	AHU & PAU Function Test	30 days	Sun 24/6/18	Mon 23/7/1	
3	Ventilating Fans Function Test	30 days	Sun 24/6/18	Mon 23/7/1	18
4	Vehicle Extraction System Function Test	30 days	Mon 25/6/18	Tue 24/7/1	
5	Welding Extraction System Function Test	30 days	Mon 2/7/18	Tue 31/7/1	
56 57	VRV Unit Function Test	30 days	Tue 10/7/18 Sun 1/7/18	Wed 8/8/1 Mon 30/7/1	
58	Bio-oxygen Generator Function Test Ultra Violet Sterilizing Light Function Test	30 days 30 days	Wed 4/7/18	Thu 2/8/1	
59	Ductwork Leakage Test	73 days	Mon 28/5/18	Wed 8/8/1	
50	Air Balancing and Flow Measurement	30 days	Tue 24/7/18	Wed 22/8/1	
51	Air Duct Cleaning	14 days	Tue 24/7/18	Mon 6/8/1	18
52	IAQ Measurement	14 days	Sat 28/7/18	Fri 10/8/1	
53 54	Motor Control Cubicles (MCC) Factory Test	7 days	Wed 27/12/17	Tue 2/1/1	
55	Motor Control Cubicles (MCC) Site Test CCMS Functional Test	7 days 30 days	Thu 29/3/18 Sun 24/6/18	Wed 4/4/1 Mon 23/7/1	
6	VAC Functional Test	30 days	Sun 27/5/18	Mon 25/6/1	
57	N.C. Measuring Test	30 days	Tue 24/7/18	Wed 22/8/1	
58	Room temperature Measuring Test	30 days	Tue 24/7/18	Wed 22/8/1	
59	Function Test for Condensate Drain Pipe	30 days	Tue 10/7/18	Wed 8/8/1	
0	PCO performanance test	30 days	Mon 2/7/18	Tue 31/7/1	
± .	Fire services installations (see also detail programme for FS trade)	726 days	Fri 5/8/16	Tue 31/7/1	18
2	Drawing Submisssion and Approval (details refer	180 days	Sun 1/1/17	Thu 29/6/1	17
-	to submission schedule)	100 udys	Jun 1/1/1/	111u 29/0/1	'
3	Equipment & Material Submisssion and Approval	180 days	Sun 25/9/16	Thu 23/3/1	17
	(details refer to submission schedule)				_
4	Approval of GBP(Initial) by FSD & WSD	21 days	Fri 5/8/16	Thu 25/8/1	
5	Submission/Application of form WWO 046(Part I	76 days	Mon 26/6/17	Sun 10/9/1	17
6	& II) for F.S. Installation	1 ,1	Cat 2/2/10	Cot 2/2/4	10
5	Submission of form WWO 046(Part IV) for F.S. Installation	1 day	Sat 3/3/18	Sat 3/3/1	IÓ
7	Submission of Drawing for D.G. Liscence to FSD	60 days	Mon 17/10/16	Thu 15/12/1	16
	for Approval	50 0035			1
8	Final Submission of Form314(Layout) &	1 day	Thu 12/7/18	Thu 12/7/1	18
	Form501(FS related) to FSD			_	_
9	Concealed Conduit & Builder Work for FS.	199 days	Sun 10/9/17	Tue 27/3/1	
L	G/F to R/F F.S. Installation - First fixing	210 days	Sun 10/9/17 Sun 10/9/17	Sat 7/4/1 Sun 10/9/1	
	Application of Direct Telephone Link Handover of G/F F.S. Transfer Pump Rm. for F.S.	1 day 1 day	Thu 15/3/18	Thu 15/3/1	
	Installation	i day	110 13/3/10	mu 13/3/1	
3	F.S. Installation in F.S. Transfer Pump Rm.	70 days	Fri 16/3/18	Thu 24/5/1	18
4	Handover of G/F F.S. Control Rm. for F.S.	1 day	Mon 12/3/18	Mon 12/3/1	_
	Installation				
	F.S. control panel Installation in F.S. control Rm.	60 days	Tue 13/3/18	Fri 11/5/1	
,	G/F FS Installation	42 days	Mon 21/5/18	Sun 1/7/1	
3	UG/F FS Installation 1/F FS Installation	50 days 50 days	Mon 16/4/18 Mon 30/4/18	Mon 4/6/1 Mon 18/6/1	
,)	2/F FS Installation	50 days	Thu 3/5/18	Thu 21/6/1	_
7 I.			Sat 5/5/18	Sat 23/6/1	
-	3/F FS Installation	50 days	30(3/3/10		

Remarks: *Delay in selection of pile for loading test and Special ground conditions subject to EOT claim 7-13 Feb 2016 and 27 Jan- 2 Feb 2017 and 16 Feb - 19 Feb 2018 Chinese New Year site close

Page 8

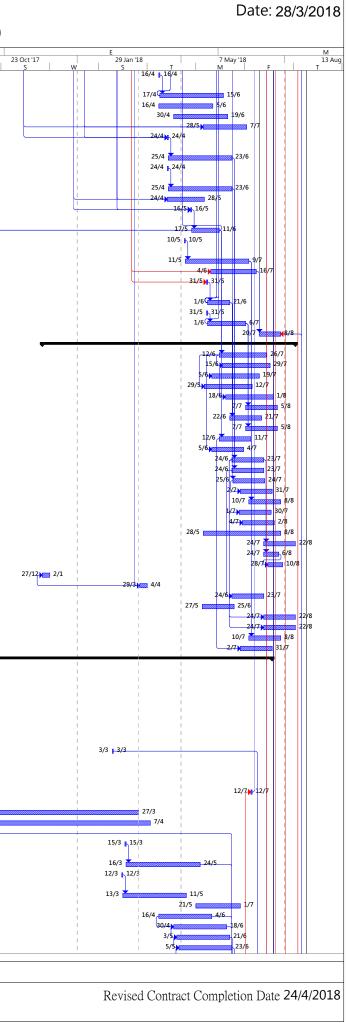

China Road and Bridge Corporation

Master Construction Programme (Rev.13)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road (SSD505)

	lame	Duration	Start	Finish _
91 4/F	FS Installation	50 days	Mon 7/5/18	Mon 25/6/18
	F FS Installation	50 days	Mon 14/5/18	Mon 2/7/18
	ndover of SPR. & F.S. Pump Rm. for F.S. stallation	0 days	Thu 31/5/18	Thu 31/5/18
	S. Installation in SPR. & F.S. Pump Rm.	30 days	Thu 31/5/18	Fri 29/6/18
	S. Final fixing	24 days	Sun 24/6/18	Tue 17/7/18
96 Wa	ater Authority inspections for FS Installation	7 days	Wed 18/7/18	Tue 24/7/18
	tain Water Certificate	7 days	Wed 25/7/18	Tue 31/7/18
98 FS	inspection for DG Stores (1st)	7 days	Fri 15/6/18	Thu 21/6/18
	inspection for DG Stores (2nd)	14 days	Fri 22/6/18	Thu 5/7/18
	tained DG. Licence	7 days	Fri 6/7/18	Thu 12/7/18
	sting & Commissioning (FS)	75 days	Fri 18/5/18	Tue 31/7/18
	Hydraulic Test for Pipework	21 days	Mon 18/6/18	Sun 8/7/18
03	G/F & UG/F	21 days	Mon 18/6/18	Sun 8/7/18
04	1/F	21 days	Mon 18/6/18	Sun 8/7/18
05	2/F	21 days	Mon 18/6/18	Sun 8/7/18
06	3/F	21 days	Mon 18/6/18	Sun 8/7/18
07	4/F	21 days	Mon 18/6/18	Sun 8/7/18
08	R/F	21 days	Mon 18/6/18	Sun 8/7/18
	Equipment Performance Test	30 days	Fri 18/5/18	Sat 16/6/18
10	G/F & UG/F		Mon 2/7/18	
10	1/F	30 days		Tue 31/7/18
12		30 days	Mon 25/6/18	Tue 24/7/18
12	2/F	30 days	Mon 25/6/18	Tue 24/7/18
13	3/F 4/F	30 days	Mon 25/6/18	Tue 24/7/18
14		30 days	Mon 2/7/18	Tue 31/7/18
	R/F	30 days	Mon 2/7/18	Tue 31/7/18
	Interfacing test with AC/EE/Lift/Fire Shutter etc.	2 days	Wed 18/7/18	Thu 19/7/18
WICCI	hanical handling and lifting installation	533 days	Mon 27/2/17	Mon 13/8/18
to s	awing Submisssion and Approval (details refer submission schedule)	45 days	Mon 27/2/17	Wed 12/4/17
(de	uipment & Material Submisssion and Approval etails refer to submission schedule)	60 days	Mon 6/3/17	Thu 4/5/17
	ondola system	138 days	Sun 25/3/18	Thu 9/8/18
	Cast-in bolt	27 days	Sun 25/3/18	Fri 20/4/18
	Guide rail installation	21 days	Thu 31/5/18	Wed 20/6/18
	Gondola system installation	42 days	Thu 21/6/18	Wed 1/8/18
	T&C for gondola	8 days	Thu 2/8/18	Thu 9/8/18
	issor platform	57 days	Mon 18/6/18	Mon 13/8/18
	Installation	50 days	Mon 18/6/18	Mon 6/8/18
	T&C for scissor platform	7 dovic	Tue 7/8/18	Mon 13/8/18
		7 days		
28 Lift ((by Nominated Subcontractor)	839 days	Wed 13/4/16	Mon 30/7/18
28 Lift (29 No		839 days 1 day	Wed 13/4/16 Wed 13/4/16	Mon 30/7/18 Wed 13/4/16
28 Lift (29 No	(by Nominated Subcontractor)	839 days	Wed 13/4/16	Mon 30/7/18
 28 Lift (29 No 30 Dra 40 store 	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule)	839 days 1 day 46 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16
 28 Lift (29 No 30 Dra 31 Ma 	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer	839 days 1 day	Wed 13/4/16 Wed 13/4/16	Mon 30/7/18 Wed 13/4/16
 ¹⁸ Lift (¹⁹ Noi ¹⁰ Dratic state ¹⁰ Ma 	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule)	839 days 1 day 46 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16
 28 Lift (29 Not 30 Dra 30 to s 31 Ma 32 Equ (de 	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) nnufacturing & Shipment ujment & Material Submisssion and Approval etails refer to submission schedule)	839 days 1 day 46 days 181 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17
 28 Lift (29 Not 30 Dra to s 31 Ma 32 Equidate 33 Hat 	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) nufacturing & Shipment uipment & Material Submisssion and Approval	839 days 1 day 46 days 181 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17
 8 Lift (9 Notes 0 Drates 1 Ma 2 Equivalence 3 Hates 	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) nnufacturing & Shipment ujment & Material Submisssion and Approval etails refer to submission schedule)	839 days 1 day 46 days 181 days 60 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17
8 Lift (9 Noi 0 Dratics 1 Ma 2 Equidation 3 Hai 4 Insprove	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) inufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) indover of lift shafts and machine rooms to NSC	839 days 1 day 46 days 181 days 60 days 31 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18
8 Lift (9 Noi 0 Dra 1 Ma 2 Equ 3 Hai 4 Ins 5 Sul	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) indover of lift shafts and machine rooms to NSC itallation, T&C (Details subject to NSC's	839 days 1 day 46 days 181 days 60 days 31 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18
8 Lift (9 Noi 0 Dra 1 Ma 2 Equ (de 3 Hai 4 Ins pro 5 Sul	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval tails refer to submission schedule) indover of lift shafts and machine rooms to NSC sallaltion, T&C (Details subject to NSC's ogramme)	839 days 1 day 46 days 181 days 60 days 31 days 70 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 9/7/18
8 Lift (9 Noi 0 Dratics 10 S 11 Mai 2 Equidation 3 Hai 4 Ins 55 Suli 6 EM 7 Ob	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) nurfacturing & Shipment uipment & Material Submission and Approval tails refer to submission schedule) ndover of lift shafts and machine rooms to NSC tallation, T&C (Details subject to NSC's gramme) bmission of Form 5	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 9/7/18 Mon 2/7/18
28 Lift (29 Noi 29 Noi 30 Dra to s to s 31 Ma 32 Equidation (delation) 33 Hai 34 Ins pro Sull 35 Sull 36 EM 37 Ob 38 I	(by Nominated Subcontractor) miniation of lift subcontractor awing Submisssion and Approval (details refer submission schedule) nunfacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) ndover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ogramme) bmission of Form 5 ISD Inspection	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 9/7/18 Mon 2/7/18 Sun 8/7/18
28 Lift (29 Noi 29 Noi 30 Dra 10 S 31 Ma 32 Equidation 33 Hai 34 Ins pro Sul 36 EM 37 Ob 38 L 39 L	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's gramme) bmission of Form 5 SD Inspection ital lift certificate	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 5/6/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 9/7/18 Mon 2/7/18 Sun 8/7/18 Mon 30/7/18
28 Lift (29 Noi 29 Noi 300 Dra 301 Dra 302 Equ 311 Ma 322 Equ (de Ba 33 Hai 34 Ins 355 Suli 36 EM 37 Ob 38 L 39 L	(by Nominated Subcontractor) minition of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submission and Approval etails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallaltion, T&C (Details subject to NSC's ogramme) bmission of Form 5 MSD Inspection tain lift certificate Lift certificate Obtained (L3, Fireman's Lift)	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 156 days 56 days 14 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 5/6/18 Tue 17/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 9/7/18 Mon 2/7/18 Mon 30/7/18 Mon 30/7/18
28 Lift (29 Noi 29 Noi 30 Dra 10 To s 31 Ma 32 Equidation (de Ba 33 Hai 34 Ins pro Suli 36 EM 37 Obb 38 L 39 L 40 L	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) nurfacturing & Shipment uipment & Material Submission and Approval tails refer to submission schedule) ndover of lift shafts and machine rooms to NSC tallation, T&C (Details subject to NSC's gramme) bmission of Form 5 MSD Inspection tail retrificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L6, Fireman's Lift)	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 56 days 14 days 14 days 14 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 5/6/18 Tue 17/7/18 Tue 17/7/18 Tue 10/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/4/18 Mon 2/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18
28 Lift (29 Noi 29 Noi 300 Dra 10 s 10 s 31 Mai 32 Equidation 33 Hai 34 Ins 35 Sui 366 EM 19 L 39 L 30 L 31 Hai	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval tails refer to submission schedule) ndover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ogramme) bmission of Form 5 MSD Inspection stain lift certificate Lift certificate Lift certificate Obtained (L3, Fireman's Lift)	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 5/6/18 Tue 17/7/18 Tue 17/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18
88 Lift (199 Noi 100 Drain 11 Ma 12 Eq. (de 133 Hai 144 Ins 155 Sulution 166 EMM 177 Ob 188 L 199 L 100 L 114 L	(by Nominated Subcontractor) minition of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval tails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ogramme) bmission of Form 5 MSD Inspection tain lift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L6, Fireman's Lift) Lift certificate Obtained (L1, Fireman's Lift) Lift certificate Obtained (L1, Fireman's Lift) Lift certificate Obtained (L1, Fireman's Lift)	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 14 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18 Tue 1/5/18 Tue 5/6/18 Tue 5/6/18 Tue 17/7/18 Tue 10/7/18 Tue 10/7/18 Tue 10/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 9/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18
8 Lift (9 Noi 0 Dra 10 Ma 1 Ma 2 Eq(de) 3 Hai 4 Ins pro 5 5 Suli 6 EM 7 Ob 8 L 9 L 0 L 1 L 2 Eq 3 Beam	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) inufacturing & Shipment uipment & Material Submisssion and Approval tails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ogramme) bmission of Form 5 ISD Inspection Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift)	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 120 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/9/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 5/6/18 Tue 17/7/18 Tue 10/7/18 Tue 10/7/18 Tue 10/7/18 Mon 7/8/17	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18
B Lift (Ø Noi Ø Dra to s Dra to s Equal 4 Ma 8 Hai 4 Ins pro Sui 5 EMM 7 Ob 8 L 9 L 2 L 8 Beam 4 Beam	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) nufacturing & Shipment uipment & Material Submisssion and Approval tails refer to submission schedule) ndover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ogramme) bmission of Form 5 MSD Inspection stain lift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n Plus - IEQ 6, 7 and WUP1	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 56 days 14 days 12 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/11/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 5/6/18 Tue 17/7/18 Tue 17/7/18 Tue 10/7/18 Sun 3/12/17	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18
8 Lift (9 Noi 0 Dratical (1 Ma 2 Equation (3 Hata 4 Ins 5 Sul 6 EM 7 Ob 8 L 9 L 0 L 1 L 2 L 3 Beam 4 Beam 5 FSD	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) inufacturing & Shipment uipment & Material Submisssion and Approval tails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ogramme) bmission of Form 5 ISD Inspection Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift)	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 120 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/9/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 5/6/18 Tue 17/7/18 Tue 10/7/18 Tue 10/7/18 Tue 10/7/18 Mon 7/8/17	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18
28 Lift (29 Noi 30 Dra 40 To 40 S 31 Mai 32 Equiparticity 33 Hai 34 Ins 34 Ins 35 Sulu 36 EM 37 Ob 38 L 39 L 40 L 12 L 13 Beam 14 Beam 15 FSDI 5 SCCU	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's opgramme) bmission of Form 5 MSD Inspection tatal lift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n Plus - FA Submission n Plus - FA Submission n Plus - FO and WUP1 inspection and Issuance of Certificate (After U Inspection)	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 14 days 120 days 7 days 21 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/1/17 Sat 31/3/18 Tue 1/5/18 Tue 1/5/18 Tue 1/5/18 Tue 5/6/18 Tue 10/7/18 Tue 10/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 9/7/18 Mon 2/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18
28 Lift (29 Noi 30 Dra 30 Dra 30 Dra 30 Dra 30 Dra 30 Dra 31 Mai 32 Equ (del Sup 33 Hai 33 Hai 33 Hai 36 EM 37 Ob 38 L 40 L 41 L 42 L 43 Beam 45 FSD i SCCC SCC 46 FS	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval tails refer to submission schedule) indver of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ogramme) bmission of Form 5 MSD Inspection tain lift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n Plus - FA Submission n Plus - IEQ 6, 7 and WUP1 inspection uspection	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 120 days 7 days 21 days 7 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 1/5/18 Tue 1/7/18 Tue 10/7/18 Tue 10/7/18 Tue 10/7/18 Tue 10/7/18 Mon 7/8/17 Sun 3/12/17 Thu 2/8/18 Thu 2/8/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/4/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 4/12/17 Sat 9/12/17 Wed 22/8/18
28 Lift (29 Noi 30 Dra 1030 Dra 1030 Dra 11 Ma 32 Equ (de ga 33 Ha 344 Ins 97 Ob 36 EM 37 Ob 38 L 40 L 41 L 42 L 43 Beam 44 Beam 45 FSD i FSD i SCCL 46 FSS 47 FS	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's gramme) bmission of Form 5 ISD Inspection itil certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n Plus - FA Submission n Plus - FA Submission D Inspection D Inspection (1st) D Inspection (20, 7 and WUP1	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 14 days 14 days 14 days 14 days 14 days 14 days 14 days 120 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/11/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 1/5/18 Tue 5/6/18 Tue 10/7/18 Tue 3/12/17 Thu 2/8/18 Thu 2/8/18 Thu 2/8/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/4/18 Mon 20/7/18 Mon 20/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18
28 Lift (29 Noi 300 Dra 1030 Tra 303 Hai 31 Mai 32 Equiparticity 33 Hai 33 Hai 344 Inss 355 Suid 366 EMM 37 Ob 38 L 37 Ob 38 L 399 L 410 L 411 L 412 L 414 Beann 415 FSD I SCCCI FSD I SCCI 466 FSS 88 Ob Scool	(by Nominated Subcontractor) mination of lift subcontractor awing Submission and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submission and Approval etails refer to submission schedule) nodover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ggramme) bmission of Form 5 MSD Inspection stall ift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n plus - FA Submission n plus - FA Submission n plus - IEQ 6, 7 and WUP1 inspection (1st) D inspection (2nd) utained FS certificate	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 14 days 14 days 14 days 14 days 14 days 14 days 14 days 120 days 7 days 7 days 7 days 7 days 7 days 7 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sun 2/10/16 Sat 1/4/17 Sun 2/9/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 1/5/18 Tue 5/6/18 Tue 10/7/18 Tue 10/7/18 Tue 10/7/18 Mon 7/8/17 Sun 3/12/17 Thu 2/8/18 Thu 2/8/18 Thu 2/8/18 Thu 16/8/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/4/18 Mon 20/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Won 23/7/18 Won 23/7/18 Won 4/12/17 Wed 22/8/18 Wed 15/8/18 Wed 15/8/18
28 Lift (29 Noi 30 Dra 40 Tra 40 S 31 Mai 32 Equiparticity 33 Hai 34 Ins 35 Suit 35 Suit 36 EM 37 Ob 38 L 39 L 40 L 12 L 13 Beam 14 Beam 15 FSDL 16 FS 17 FS 18 Ob 18 Ob	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's opgramme) bmission of Form 5 MSD Inspection fsD Inspection tain lift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n Plus - FA Submission n Plus - IEQ 6, 7 and WUP1 inspection (1st) D inspection (1st) D inspection (1st) D inspection (2sd) tained FS certificate dination & grant access to EMSD's contractor	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 14 days 14 days 14 days 14 days 14 days 14 days 14 days 120 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 29/11/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 1/5/18 Tue 5/6/18 Tue 10/7/18 Tue 3/12/17 Thu 2/8/18 Thu 2/8/18 Thu 2/8/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/4/18 Mon 20/7/18 Mon 20/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18
28 Lift (29 Noi 30 Dra 30 Dra 30 State 31 Ma 32 Equ (de State 33 Hai 34 Ins 35 Suid 36 EM 37 Ob 38 L 40 L 42 L 43 Bean 44 Bean 45 FSD i SCCC FSD k SCCC 48 Ob Que to	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval tails refer to submission schedule) indover of lift shafts and machine rooms to NSC tailalation, T&C (Details subject to NSC's ogramme) bmission of Form 5 MSD Inspection tain lift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n Plus - FA Submission </td <td>839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 120 days 7 days 30 days</td> <td>Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 1/5/18 Tue 10/7/18 Mon 7/8/17 Sun 3/12/17 Thu 2/8/18 Thu 2/8/18 Thu 16/8/18 Wed 1/8/18</td> <td>Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/7/18 Mon 2/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23</td>	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 120 days 7 days 30 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 1/5/18 Tue 10/7/18 Mon 7/8/17 Sun 3/12/17 Thu 2/8/18 Thu 2/8/18 Thu 16/8/18 Wed 1/8/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/7/18 Mon 2/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23
28 Lift (29 Noi 30 Dra to s (to s) 31 Ma 32 Equivaliant 33 Halas 34 Ins 35 Suli 36 EIM 37 Ob 38 L 39 L 440 L 43 Bean 44 Bean 44 Bean 45 FSD scct 547 FSS 48 Ob 49 Correforing 50 SCCL	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) indover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's gramme) bmission of Form 5 ISD Inspection tatin lift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission D inspection (St)	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 14 days 14 days 120 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days 7 days 30 days 40 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/1/18 Tue 1/5/18 Tue 10/18 Tue 10/7/18 Mon 7/8/17 Sun 3/12/17 Thu 2/8/18 Thu 2/8/18 Thu 16/8/18 Wed 1/8/18 Mon 9/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/4/18 Mon 20/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 41/2/17 Sat 9/12/17 Wed 22/8/18 Wed 15/8/18 Wed 15/8/18 Thu 30/8/18 Fri 17/8/18
28 Lift (29 Noi 30 Dra to s to s 31 Mai 32 Equiparticity 33 Hai 34 Ins 35 Suidation 36 EMM 37 Ob 38 L 39 L 40 L 41 L 42 L 43 Bean 44 Bean 45 FSD i SCCC 46 47 FSS 48 Ob 49 Corregion (no finity) 60 SCCC 50 SCCC 50 SCCC	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) nodover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ggramme) bmission of Form 5 SD Inspection stall ift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n plus - IEQ 6, 7 and WUP1 inspection (1st) D inspection (1st) D inspection (2nd) tained FS certificate dination & grant access to EMSD's contractor stallation of equipment U Pre-inspection U Inspection	839 days 1 day 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 14 days 14 days 14 days 14 days 14 days 120 days 7 days 7 days 7 days 7 days 7 days 30 days 8 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 1/5/18 Tue 10/7/18 Tue 10/7/18 Tue 10/7/18 Mon 7/8/17 Sun 3/12/17 Thu 2/8/18 Thu 16/8/18 Wed 1/8/18 Mon 9/7/18 Thu 2/8/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 20/7/18 Mon 20/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Won 23/7/18 Won 23/7/18 Won 23/7/18 Mon 2
28 Lift (29 Noi 30 Dra 40 Tra 40 Tra 32 Equidation 33 Hai 34 Ins 35 Sui 36 EM 37 Ob 38 Li 39 Li 41 Li 42 Li 43 Bean 44 Bean 45 FSDi 5 SCCI 46 FS 47 FS 48 Ob 90 Corror 60 SCCI 50 SCCI 51 SCCI 52 Gene	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) nodover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ggramme) bmission of Form 5 ISD Inspection tatin lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n Plus - FA Submission n Plus - Secutificate U Inspection (1st) D inspection (1st) D inspection (1st) D inspection (1st) U Inspection U Inspection U Inspection U I	839 days 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 56 days 14 days 14 days 14 days 14 days 14 days 120 days 7 days 7 days 7 days 7 days 30 days 40 days 8 days 28 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/1/17 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 5/6/18 Tue 10/7/18 Tue 10/8/18 Wed 1/8/18 Won 9/7/18 Tue 23/8/18 Fri 27/7/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 30/7/18 Mon 2/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23
28 Lift (29 Noi 30 Dra 40 To s 31 Mai 32 Equ (del Sci 33 Hai 34 Ins 33 Hai 34 Ins 35 Sci 36 EM 37 Ob 38 L 39 L 40 L 41 Bean 42 L 43 Bean 44 Bean 45 FSC I SCCI SCCI 50 SCCI 51 SCCI 52 Gene 53 Gene 53 Gene	(by Nominated Subcontractor) mination of lift subcontractor awing Submisssion and Approval (details refer submission schedule) unufacturing & Shipment uipment & Material Submisssion and Approval etails refer to submission schedule) nodover of lift shafts and machine rooms to NSC stallation, T&C (Details subject to NSC's ggramme) bmission of Form 5 SD Inspection stall ift certificate Lift certificate Obtained (L3, Fireman's Lift) Lift certificate Obtained (L4, Fireman's Lift) Lift certificate Obtained (L5, Fireman's Lift) Lift certificate Obtained (L1, L2) n Plus - FA Submission n plus - IEQ 6, 7 and WUP1 inspection (1st) D inspection (1st) D inspection (2nd) tained FS certificate dination & grant access to EMSD's contractor stallation of equipment U Pre-inspection U Inspection	839 days 1 day 1 day 46 days 181 days 60 days 31 days 70 days 0 days 0 days 0 days 14 days 14 days 14 days 14 days 14 days 120 days 7 days 7 days 7 days 7 days 7 days 30 days 8 days	Wed 13/4/16 Wed 13/4/16 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 1/4/17 Sun 2/10/16 Sat 31/3/18 Tue 1/5/18 Mon 2/7/18 Sun 8/7/18 Tue 1/5/18 Tue 10/7/18 Tue 10/7/18 Tue 10/7/18 Mon 7/8/17 Sun 3/12/17 Thu 2/8/18 Thu 16/8/18 Wed 1/8/18 Mon 9/7/18 Thu 2/8/18	Mon 30/7/18 Wed 13/4/16 Wed 16/11/16 Thu 28/9/17 Wed 29/3/17 Mon 30/4/18 Mon 20/7/18 Mon 20/7/18 Mon 30/7/18 Mon 30/7/18 Mon 30/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Mon 23/7/18 Won 23/7/18 Won 23/7/18 Won 23/7/18 Mon 2


Project: SSD505 - Master Construction Date: Wed 28/3/18

Task

Progress Milestone

Summary


Remarks: *Delay in selection of pile for loading test and Special ground conditions subject to EOT claim 7-13 Feb 2016 and 27 Jan- 2 Feb 2017 and 16 Feb - 19 Feb 2018 Chinese New Year site close

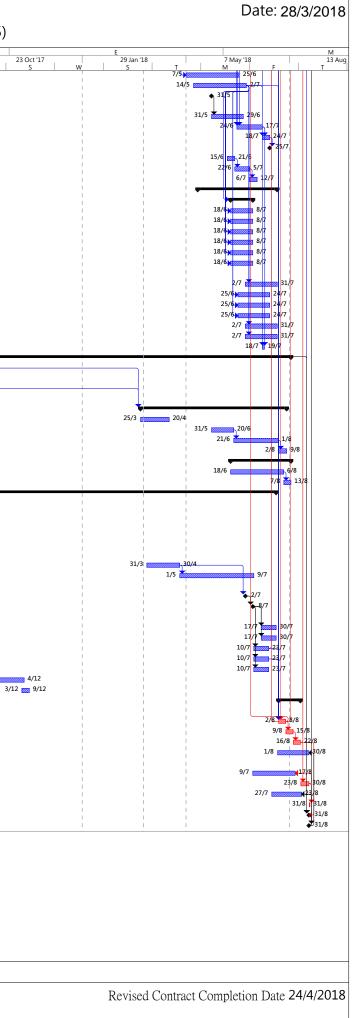

Telemax Environmental and Energy Management Limited Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com




Appendix B Organization Chart

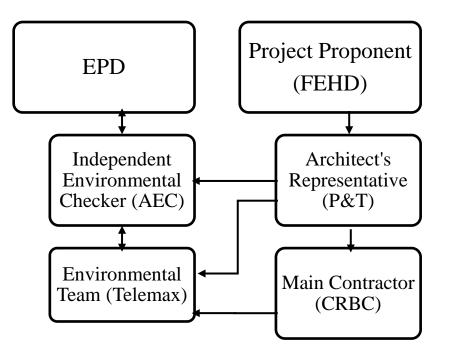



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



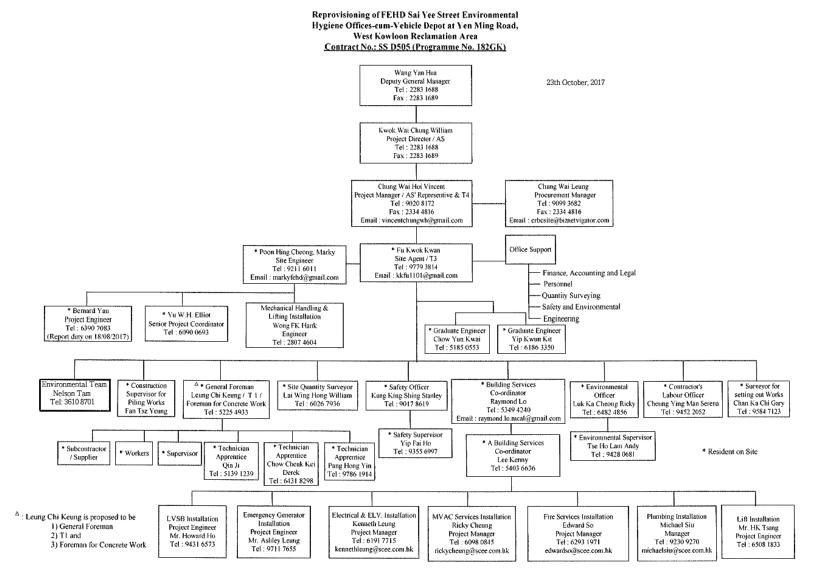

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Appendix C Implementation Schedule of Environmental Mitigation Measures (EMIS)

Air Quality – Schedule of Recommended Mitigation Measures

		Implementation Status			tion Status	
	Environmental Protection Measures	Location	Implemented	Partially Implemented	Not Implemented	Not Applicable
Air (Quality (Construction)					
•	Use of regular watering, to reduce dust emissions from exposed site surfaces and unpaved roads, particularly during dry weather;	All areas	✓			
•	Use of frequent watering for particularly dusty construction areas close to ASRs	All areas	✓			
•	Side enclosure and covering of any practicable owing to frequent usage, watering should be applied to aggregate fines;	All areas	✓			
•	Open temporary stockpiles should be avoided or covered. Prevent placing dusty material storage piles near ASRs;	All areas	✓			
•	Tarpaulin covering of all dust vehicle loads transported to, from and between site locations;	All areas				\checkmark
•	Establishment and use of vehicle wheel and body washing facilities at the exit points of the site;	All areas	✓			
•	Imposition of speed controls for vehicle son unpaved site roads. 8 km/hr is the recommended limit;	All areas	√			
•	Routing of vehicles and positioning of construction plant should be at the maximum possible distance from ASRs;	All areas	✓			
•	Every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA), if applicable, should be covered entirely buy impervious sheeting or placed in an area sheltered on the top and the 3-sides; and	All areas	✓			
•	Loading, unloading, transfer, handling or storage of large amount of cement or dry PFA should be carried out in a totally enclosed system or facility, and nay vent or exhaust should be fitted with the an effective fabric filter or equivalent air pollution control system.					✓
•	3-sides enclosed washing bays and maintenance workshops, served with mechanical ventilations to maintain all the time with proper negative air pressure.	Washing bays & maintenance workshops				✓
•	Deodorization system such as active carbon filters or chemical scrubber (or equivalent) will be applied at the ventilation duct prior to discharging to the atmosphere, having odor removal efficiency of 85% or above at normal operation, and under regular and proper maintenance and replacement.	Washing				✓
•	Commissioning test requirement should be incorporated in the specification during commissioning period order to ensure the odor removal efficiency (at least 85%) of the proposed odor removal unit.	Washing				✓
•	Monitoring test on odor removal efficiency of the odor removal unit should be carried out quarterly in the first year of operation. Development of monitoring and investigation plan, as well as work procedure, prior to operation of the unit is recommended.	Washing bays & maintenance workshops				✓





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Noise – Schedule of Recommended Mitigation Measures

		- ,.	Implementation Status				
	Environmental Protection Measures	Location	Implemented	Partially Implemented	Not Implemented	Not Applicable	
•	Carefully arrange the timing and sequencing of the various construction activities according to the actual site work situation;	All areas	~				
•	Limit the quantity of PME to be operated concurrently and their proportion of usage were recommended in the Project and incorporated in the Noise Impact Assessment;	All areas	~				
•	The proposed quantity of PMEs and their proportion of usage should be confirmed feasible by the Engineer;	All areas	✓				
•	In the case during school examination, more stringent construction noise criteria should be imposed, the potentially most disruptive construction activities should be avoided, and arranged to be conducted during school holidays as far as practicable.	All areas	~				
•	The use of Sound Power Levels (SWLs) for typical PME provided in the GWTM and that for equivalent "quiet" plants: Loader, wheeled (Back-hoe)Excavator, Tracked Generator Mobile Crane 	All areas	1				
•	 The use of temporary noise barriers if applicable: Movable barriers with skid footing and a small cantilevered upper portion Noise jacket/muffler Applicable PME with temporary noise barriers: excavator and mobile crane Selection of insulation material: acoustic mats 	All areas	¥				
•	 The use of temporary noise barriers if applicable Movable barriers with skid footing and a small cantilevered upper portion Noise jacket/muffler Applicable PME with temporary noise barriers: excavator and mobile crane Selection of insulation material: acoustic mats 	All areas	1				
•	Only well-maintained plant should be operated on-site and plants should be operated on-site and plants should be serviced regularly during the construction period;	All areas	~				
•	Mobile plant, if any, should be sited as gar from NSRs as possible;	All areas	✓				
•	Plant known to emit noise strongly in one direction should, wherever possible, be properly oriented so that the noise is directed away from the nearby NSRs;	All areas	~				
•	Use of site hoarding as a noise barrier to screen noise at low level NSRs;	All areas	✓				
•	Machines and plant that may be in intermittent use should be shut down between works periods or should be throttled down to a minimum;	All areas	~				
•	Any material stockpiles and other structures should be effectively utilised, wherever practicable, to screen the noise from on-site construction activities	All areas	~				
•	The Workshop Vehicle Repair Activities should be carried out under the covered area of the Transport Workshop Section on the G/F as the building of FEHD Depot itself provides screening effect to the NSRs	Transport Workshop Section				✓	
•	The workshop vehicle repair activities should not be carried out during night-time period	Transport Workshop Section				✓	
•	Acoustic treatment, such as acoustic louvres, silencers, enclosures could be applied to achieve noise attenuation on the use of MVAC and other Building Service Equipment so that the SWL of the equipment shall not exceed the specified "maximum allowable SWL" in various plant rooms.	Transport Workshop Section				✓	





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Water Quality – Schedule of Recommended Mitigation Measures

	Environmental Protection Measures		Implementation Status				
	Environmental Protection Measures	Location	Implemented	Partially Implemented	Not Implemented	Not Applicable	
Water Qua	ality and Sewerage						
cons Char be p syste	he establishment of works site, perimeter cut-off drains to direct offsite water around the Site should be structed with internal drainage works and erosion and sedimentation control facilities implemented. nnels) both temporary and permanent drainage pipes and culverts), earth bunds or sand bag barriers should provided to divert the stormwater to silt removal facilities. The design of the temporary on-site drainage em will be undertaken by the Contractor prior to the commencement of construction;	All areas	4				
Temp throu chan	es or embankments for flood protection should be implemented around the boundaries of earthworks areas. porary ditches should be provided to facilitate the run-off discharge into an appropriate watercourse, ugh a silt / sediment trap. Silt / sediment traps should also be incorporated in the permanent drainage unels to enhance deposition rates;	All areas	*				
1/94 cond basir	design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN, which states that the retention time for silt / sand traps should be 5 minutes under maximum flow litions. The sizes may vary depending upon the flow rate, but for a flow rate of 0.1m^3 /s, a sedimentation n of 30m^3 would be required and for a flow rate of 0.5m^3 /s the basin would be 150m^3 . The detailed design of sand / silt traps should be undertaken by the Contractor prior to the commencement of construction;	All areas				√	
(Apr days sease	construction works should be programmed to minimize surface excavation works during rainy seasons ril to September), as soon as possible after the earthworks have been completed, or alternatively, within 14 of the cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy on, or at any time of year when rainstorms are likely, exposed slope surfaces should be covered by tarpaulin ther means;	All areas	1				
flow adva incle	overall slope of works sites should be kept to a minimum to reduce the erosive potential of surface water rs, and all trafficked areas and access roads should be protected by coarse stone ballast. An additional intage accruing from the use of crushed stone is the positive traction gained during the prolonged periods of ement weather and the reduction of surface sheet flows;	All areas	1				
to en grits	drainage facilities and erosion and sediment control structures should be regularly inspected and maintained nsure their proper and efficient operation at all times particularly following rainstorms. Deposited silts and should be removed regularly and disposed of by spreading evenly over stable, vegetated areas;	All areas	*				
in we pump facili		All areas	1				
with cons	open stockpiles of construction materials (for example, aggregates, sand and fill material should be covered tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of struction materials, soil, silts or debris into any drainage system;	All areas	*				
to pr direc	holes (including newly constructed ones) should always be adequately covered and temporarily sealed so as revent silt, construction materials or debris being washed into the drainage system and storm run-off being cted into foul sewers;	All areas	*				
is im	autions to be taken at any time of the year when rainstorms are likely actions to be taken when a rainstorm iminent or forecasted and during or after rainstorms, are summarized in Appendix A2 of ProPECC PN 1/94. icular attention should be paid to the control of silty surface run-off during storm events;	All areas	*				
• All v	vehicles and plant should be cleaned before leaving the Site to ensure no earth, mud, debris and the like is	All areas	✓				

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

	deposited by them on roads.				
•	Oil interceptors should be provided in the drainage system downstream of any oil / fuel pollution sources. Oil interceptors should be emptied and cleaned regularly to percent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for oil interceptors to prevent flushing during heavy rain;	All areas	~		
•	Oil interceptors should be provided in the drainage system downstream of any oil / fuel pollution sources. Oil interceptors should be emptied and cleaned regularly to percent the release of oil and grease into the storm water drainage system after accidental spillage. A bypass should be provided for oil interceptors to prevent flushing during heavy rain;	All areas	4		
•	All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to percent spilled fuel oils from reaching the nearby WSRs.		~		
•	Application to the EPD for a discharge licence for discharge of effluent from the construction site under the WPCO. The discharge quality must meet the requirements specified in the discharge license.	All areas	~		
•	All the run-off and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the Technical Memorandum.	All areas	✓		
•	Minimum distance of 100m should be maintained between the discharge points of construction site effluent and the existing seawater intakes.	All areas	\checkmark		
•	No new effluent discharges in nearby typhoon shelters should be allowed.	All areas	✓		
•	The beneficial uses of the treated effluent for other on-site activities such as dust suppression, wheel washing and general cleaning etc., would minimise water consumption and reduce the effluent discharge volume.	All areas	~		
•	Portable chemical toilets and sewage holding tanks are recommended for the handling of the construction sewage generated by the workforce. A licensed contractor should be employed to provide appropriate and adequate portable toilets and be responsible for appropriate disposal and maintenance.	All areas	~		
•	Any maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	All aroos	~		
•	All sewage arising from the Project should be collected and diverted to the public sewerage system via proper connections to minimise water quality impact from the operation of the Project and ensure compliance with Technical Memorandum on Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and	Office-cum- Vehicle			√
•	Coastal Water under the WPCO. To prevent the potential contaminated wastewater from entering the existing public sewerage systems, run-offs from the covered areas including the vehicle washing bays and vehicle parking space will be properly treated prior to the discharge into the sewerage system. The treated effluent for discharging into the public sewerage system should comply with the effluent standards as stated in the Technical Memorandum on Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters under the WPCO.	Office-cum- Vehicle Depot			✓
•	There is a need to apply to the EPD for a discharge licence for discharge of the operational effluent from the Project under the WPCO. The discharge quality must meet the requirements specified in the discharge licence.	The Office-cum- Vehicle Depot			~



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Waste – Schedule of Recommended Mitigation Measures

	Environmental Protection Measures		Implementation Status				
	Environmental Protection Measures	Location	Implemented	Partially Implemented	Not Implemented	Not Applicable	
Was	te Management and Land Contamination						
•	The requirements as stipulated in the ETWB TC(W) No. 19/2005 "Environmental Management on Construction Sites" and the other relevant guidelines should be included in the Particular Specification for the Contractor as appropriate. Contractor should be required to implement the recommended waste management measures through establishing a Waste Management Plan (WMP) in accordance with the ETWB TC(W) No.19/2005 so as to provide an overall framework of waste management and reduction. The WMP should be submitted to the Project/Site Engineer prior to the construction commencement of the Project for approval and include the followings: Waste management policy; Record of generated waste; Waste reduction target; Waste reduction target; Role and responsibility of waste management team; Benefit of waste management; Analysis of waste materials; Reuse, recycling and disposal plans; Transportation process of waste products; and Monitoring and action plan. The waste management hierarchy below should be strictly followed. This hierarchy should be adopted to evaluate the waste management options in order to maximise the extent of waste reduction and cost reduction. The records of quantities of waste generated, recycled and disposed (location) should be properly documented	All areas	1				
•	Standard formwork or pre-fabrication should be used as far as practicable so as to minimise the C&D Materials arising. The use of more durable formwork or plastic facing for construction works should also be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should be carefully planned in order to avoid over-ordering and wastage. The Contractor should recycle as many C&D materials as possible on-site. The public fill and C&D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials. Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.	All areas	4				
•	A recording system for the amount of waste generated, recycled and disposed (locations) should be established. The future Contractor should also provide proper training to workers regarding the appropriate concepts of site cleanliness and waste management procedures, e.g. waste reduction, reuse and recycling all the time.		~				
•	All waste containers shall be in a secure area on hardstanding.	All areas	✓				
•	Training of site personnel in, site cleanliness, proper waste management and chemical handling procedures.	All areas	√				
•	Provision of sufficient waste disposal points and regular collection of waste.	All areas	√				
•	Appropriate of sufficient waste disposal points and regular collection of waste by either covering trucks or by transporting wastes in enclosed containers.	All areas	~				
•	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.	All areas	✓				
•	Separation of chemical wastes for special handling and appropriate treatment.	All areas	✓				
•	The site and surroundings shall be kept tidy and litter free.	All areas	√				

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com





	No waste shall be burnt on-site	All areas	✓		
	Make provisions in contract documents to allow and promote the use of recycled aggregates where appropriate.	All areas	√		
	Wheel washing facilities shall be used by all trucks leaving the site to prevent transfer of mud onto public roads.	All areas	✓		
	Sorting of demolition debris and excavated materials from demolition works to recover reusable/recyclable		✓		
	portions (i.e. soil, broken concrete, metal etc.).	All areas	v		
	Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse	A 11	✓		
	or recycling of materials and their proper disposal.	All areas	v		
)	Encourage collection of aluminum cans by providing separate labeled buns to enable this waste to be segregated	A 11	✓		
	from other general refuse generated by the workforce.	All areas	v		
•	Proper storage and site practices to minimize the potential for damage or contamination of construction	A 11	✓		
	materials.	All areas	v		
•	Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary	A 11	✓		
	generation of waste.	All areas	v		
•	Waste haulier must hold a valid permit for the collection of waste as stipulated in their permits, Removal of	A 11	✓		
	waste should be done in a timely manner.	All areas	v		
)	Register as a Chemical Waste Producers to the EPD	All areas	√		
)	Suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed;	All areas	√		
)	Having a capacity of <450L unless the specifications have been approved by the EPD;	All areas	√		
•	Displaying a label in English and Chinese according to the instructions prescribed in Schedule 2 of the	A 11	✓		
	Regulations;	All areas	v		
)	Clearly labelled and used solely for the storage of chemical wastes;	All areas	√		
•	Enclosed with at least 3 sides;	All areas	✓		
•	Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container of 20%	All areas	✓		
	by volume of the chemical waste stored in the area, whichever is greatest;	All aleas	•		
•	Adequate ventilation;	All areas	✓		
•	Sufficiently covered to prevent rainfall entering (water collected within the bund must be tested and disposed of	All areas	✓		
	as chemical waste, if necessary);	All areas	v		
•	Incompatible materials are adequately separated.	All areas	√		
)	Adequate numbers of portable toilet should be provide for on-site workers. Portable toilets should be maintained				
	in reasonable states, which will not deter the workers from utilizing them. Night soil should be regularly	All areas	✓		
	collected by licensed collectors.				
		The			1
•	The requirements stipulated in the Code of Practice on the Packaging. Labelling and Storage of Chemical				v
	Wastes should be followed in handling of chemical waste as in construction phase.	Vehicle			
		Depot			
,	A trip-ticket system should be operated in accordance with the Waste Disposal (Chemical Waste) (General)	The			1
	Regulation to monitor all movements of chemical wastes which would be collected by a licensed collector to a	Office-cum-			•
	licensed facility for final treatment and disposal.	venicie			
	neensed neinty for final reaction and disposal.	Depot			
		The			
•	The recommendations proposed for the mitigation of impacts from chemical waste in construction phase should				\checkmark
	also be followed.	Vehicle			
		Depot			



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



	The		1
• Provide recycling bins at designated areas for proper recycling of papers, aluminum cans and plastics bottles	Office-cum-		v
Fronde recycling on sur designated areas for proper recycling of papers, autimutin cans and phastes bottes	Vehicle		
	Depot		
	The		
Separation from other waste types and collected by licensed collectors at daily basis to minimize the potential	Office-cum-		v
impacts from odour and vermin.	Vehicle		
	Depot		
	The		1
Storage of Chemicals and Chemical Wastes	Office-cum-		•
storage of chemicals and chemical wases	Vehicle		
	Depot		
	The		1
Emergency Procedures	Office-cum-		•
	Vehicle		
	Depot		
	The		1
Spillage/leakage of Liquid Chemical/Waste at Storage Area	Office-cum-		·
Skringer reminge er zigland einennem fraste in Storager nen	Vehicle		
	Depot		
	The		1
Spillage/Leakage at Repairing and Maintenance Areas	Office-cum-		·
- L	Vehicle		
	Depot		
	The		✓
Record of Incidents	Office-cum-		
	Vehicle		
	Depot		
	The		✓
Procedures for Disposal of Wastes	Office-cum-		
1	Vehicle		
	Depot		



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



		.	Implementation Status				
	Environmental Protection Measures	Location	Implemented	Partially Implemented	Not Implemented	Not Applicable	
La	ndscape and Visual						
•	Cautiously arrangement of the operation or placement of the construction plant and machinery, and the transportation or storage of material to reduce and confined the potential adverse impacts in certain areas in the Site	All areas	1				
•	Minimise the height of temporary structures such as hoardings and site offices, and restore the temporary construction site locally to the existing condition in order to minimise any negative impacts and associated uncomfortable views.	All areas	*				
•	Check the site boundaries regularly to ensure the working area does not exceed and causes further damage to the surrounding area.	All areas	1				
•	In case of nighttime construction is conducted, control of nighttime lighting on the works areas to prevent undesired light pollution to the surrounding area, such as viewers from roads, should be implemented.	All areas				\checkmark	
•	Provision of temporary landscape treatment during construction phase, such as temporary planting around the site office, applying aesthetic treatments on site hoardings and/or façade of site office	All areas	1				
•	Provision of green roof of site office	All areas	✓				
•	Erection of fencing around the trees	All areas	√				
•	Avoidance of placing any construction materials close to the trees	All areas	\checkmark				
•	Apply mulching beyond root collar	All areas	\checkmark				
•	Conduct visual checking/monitoring in regular basis	All areas	√				
•	Proper arrangement of materials for operational activities, including vehicle repair, maintenance, operation and parking, carried out within the office-cumvehicle depot building.	All areas				\checkmark	





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Retain Tree Survey



T21





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com Appendix D Calibration Certificates







深 圳 中 航 技 术 检 测 所 SHENZHEN METROLOGY & MEASUREMENT INSTITUTE OF AVIC 中国航空工业深圳特区计量测试站 SHENZHEN METROLOGY & MEASUREMENT STATION OF CHINA AVIATION INDUSTRY 国防科技工业第一计量测试研究中心深圳计量检测站 SHENZHEN METROLOGY & MEASUREMENT STATION OF CIMM

不交 油 コー

CALIBRATION CERTIFICATE

证书编号 Certificate Number

L17AA017030003

委托单位 上峰检测认证有限公司 Client 地 址 香港荃湾海盛路3号TML广场10楼D6A室 Address 器具名称 声级计/Sound Level Meters Description 器具用途 Usage 规格型号 AWA5661 Model/Type 制造单位 杭州爱华仪器有限公司 Manufacturer 哭目编号

裔 具 编 亏 Serial No.	304042						
结 论 Conclusion	见校准结果	/Calibratio	n				
		Ш			准人 roved by	邵波沉	邵浊沉
	(证书专用年)	航技》			验员 ecked by	邵法沉	邵浊沉
	家道	(1)	N M		准员 prated by	徐小芳	徐小芳
委托日期 Received Date 校准日期 Calibration	2017 2017	交進专用 Year	音月 Minth 月 Month	21 21	日 Day 日 Day		

计量校准机构备案号(Register No.):[2013]粤量校5007号

地址:广东省深圳市福田区车公庙泰然四路劲松大厦9A、1B、105A

Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

Add: 9A-1B-105A, Jingsong Building, Tairan 4th Road, Chegongmiao, Futian District, Shenzhen, Guangdong, China 电话 (Tel):0755-83890620 83890591 传真 (Fax):0755-83890704 邮政编码 (Post Code):518040 网址 (Web):http://www.szcatci.com 电子邮箱 (E-mail):market@szcatci.com

第1页共5页 Page1of5

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Ø	深圳中航技术检测所		
中航工业	中国航空工业深圳特区计量测试站 国防科技工业第一计量测试研究中心深圳计量检测站	证书编号:	L17AA017030003

校准说明

Directions of Calibration

1本所(站)是国家法定计量检定机构,其管理体系按照JJF 1069-2012法定计量机构考核规范、ISO/IEC17025:2005和CNAS相关要求运行。

The institute/station is the Service of Legal Metrological Verification. It has implemented management system in accordance with JJF 1069-2012 Rules for the Examination of the Service of Legal Metrological Verification, ISO/IEC 17025:2005 and CNAS related requirements.

2.本次校准结果仅对被测件有效,所出具的数据均可溯源到国家或国际计量基准。

The results relate only to the items specified. All data issued by the certificate are traceable to the national or international primary standards of measurement.

3.未经本所(站)许可,不得部分复印此证书内容。

The certificate shall not be partly copied without the written approval of the institute/station.

4.参照技术依据 (Reference documents for the calibration) :

参照JJG 188-2002《声级计检定规程》《V.R.of Sound Level Meters》

5.校准地点及环境条件(Place and environmental conditions of the calibration):

地点(Place)	温度(Temperature)	相对湿度(Relative Humidity)
本所振动声学室	22.0 °C	60 %
6 大次均准确体用的主要注意提供推荐常信息 (Major stan	dand douicos usod in the solibre	tion) :

6.本次校准所使用的主要计量标准装置信息(Major standard devices used in the calibration):

计量标准名称 Description	测量范围 Range	不确定度或最大允差 或准确度等级 Uncertainty of Measurement or Maximum Permissible Errors	证书编号 Certificate No.	有效期 Due Date

7.本次校准所使用的主要计量标准器具信息(Major standards of measurement used in the calibration):

器具名称 Description	编号/型号 Serial No./Model	不确定度或最大允差 或准确度等级 Uncertainty of Measurement or Maximum Permissible Errors	证书编号 Certificate No.	有效期 Due Date
可变阻抗衰减器	2300060/984A	U=0.22dB (k=2)	WX17000302209	2018.03.30
函数信号发生器	US34020710/33120A	频幅特性:0.20dB,频率:U _{rel} =1E- 7(<i>k</i> =2)	WWS201700237	2018.04.04
测量放大器	089867/AWA5810D	\pm 0.2 dB ; \pm 0.5 dB	SSD201700243	2018.01.09
标准传声器	2172118/4190	U=0.3 dB (k=2)	SSD201606162	2017.10.13
声校准器	2292007/4231	1级	SSD201606161	2017.10.13
猝发音信号发生 器	123249/AWA5551	MPE:频率:±0.1%,失真:≤1%, 衰减: <i>U</i> =0.2dB(<i>k</i> =2)	D17AA00136000 8	2018.05.08

第2页共5页 Page 2 of 5





深圳中航技术检测所 中国航空工业深圳特区计量测试站 或取科技工业第一计量测试研究中心深圳计量检测站

证书编号:L17AA017030003

校准结果

Result of Calibration

1、外观及功能正常性检查/Appearance and function check:正常/Pass。

2、声级计指示声级/Level Calibration:

校准前示值/Indication before Calibrated: 94.0dB

校准后示值/Indication After Adjusted : 94.0dB

3、频率计权/Frequency weightings:

标称频率	允许下限	A计权	允许上限
Nominal frequency	Lower Limit	A-weighting	Upper Limit
(Hz)	(dB)	(dB)	(dB)
31.5	-42.9	-39.2	-35.9
63	-28.7	-25.3	-23.7
125	-18.1	-16.6	-14.1
250	-10.5	-8.9	-6.7
500	-5.1	-3.7	-1.3
1000 (ref.)	-1.4	0.0	+1.4
2000	-1.4	+1.5	+3.8
4000	-2.5	+2.1	+4.6


标称频率	允许下限	C计权	允许上限
Nominal frequency	Lower Limit	C-weighting	Upper Limit
(Hz)	(dB)	(dB)	(dB)
31.5	-6.5	-0.5	+0.5
63	-3.3	-0.3	+1.7
125	-2.2	-0.2	+1.8
250	-1.9	-0.1	+1.9
500	-1.9	-0.1	+1.9
1000 (ref.)	-1.4	0.0	+1.4
2000	-2.8	+0.3	+2.4
4000	-4.4	+0.5	+2.8

第3页共5页 Page 3 of 5





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



4、级线性(参考频率 1kHz)/Level linearity error(Reference frequency 1kHz) :

4.1、级程变化误差 (参考频率: 1000Hz): A计权/A-weighting

Level Change Error (Reference frequency:1000Hz)

标称值	允许下限	误差	允许上限
Nominal Value	Lower Limit	Error	Upper Limit
(dB)	(dB)	(dB)	(dB)
30	-1.0	+0.3	+1.0
40	-1.0	+0.4	+1.0
50	-1.0	+0.3	+1.0
60	-1.0	+0.5	+1.0
70	-1.0	+0.2	+1.0
80	-1.0	+0.3	+1.0
90 (ref.)		0.0	
100	-1.0	+0.4	+1.0
110	-1.0	+0.3	+1.0
120	-1.0	+0.1	+1.0

5、本机噪声/Residual noise :

A计权/A-weighting : _ 29.2_dB;

Δ6、单个猝发音响应(A计权)/Tone burst response (A-weighting)

猝发	音响应(dB)/Tone b	urst response (dl	B)
L _{AFmax} -L _A	允许范围 /Conclusion	L _{ASmax} -L _A	允许范围 /Conclusion
-0.4	+0.7~-0.9	-4.0	-3.3 ~ -4.9
-0.8	-0.2~-1.8	-7.0	-6.6~-8.2
-4.1	-3.5 ~ -6.1	-12.5	-11.8 ~ -14.4
-10.3	-9.8~-12.4	-20.3	-18.7 ~ -22.3
	L _{AFmax} -L _A -0.4 -0.8 -4.1	L _{AFmax} -L _A -0.4 -0.8 -0.2~-1.8 -4.1 -3.5~-6.1	-0.4 +0.7~-0.9 -4.0 -0.8 -0.2~-1.8 -7.0 -4.1 -3.5~-6.1 -12.5

第4页共5页 Page 4 of 5





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Ø	深	圳	中	航	技	术	检	测	所
	中日	🛯 航	호 エ	业深	圳	特区	计量	测缸	虎 站
中航工业	国防	科技:	工业第-	-计量3	则由式死	形究中/	い深切的	十量检	测站

证书编号:L17AA017030003

Δ7、重复猝发音响应 (A计权) /Response to repeated Toneburst (A-weighting)

单个猝发音持续时间 (ms) /Single tone	相邻单个猝发音持续时间(ms)	猝发音响应(dB response	
burst Last time (ms)	/Adjacent single tone burst last time (ms)	L _{AEqT} -L _A	允许范围 /Conclusion
500	2000	-7.0	-6.2~-7.8
200	800	-7.0	-6.2~-7.8
50	200	-6.9	-5.7 ~ -8.3
10	40	-6.8	-5.7~-8.3

附注: ◇关于测量结果不确定度的说明/Directions of uncertainty in the calibration :

1.依据文件/According to: JJF1059.1-2012测量不确定度评定与表示

JJF1059.1-2012 Evaluation and Expression of Uncertainty in Measurement ;

2.本次测量结果的扩展不确定度/Expanded uncertainty of measured results: U = 0.4dB ~ 1.0dB (k=2)

◇ 技术要求参照JJG 188-2002/MPE according to JJG 188-2002;

△◇ 参考IEC61672-1-2002标准/Reference standard:IEC61672-1-2002;

带"Δ"项目表示未获得CNAS认可/"Δ" expressed unattained CNAS accept

◇ 建议下次送校日期/Due to date : 2018-07-20

Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

以下空白/End of data

第5页共5页 Page 5 of 5

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

中 前		HENZHI = 国 ENZHEN 国防方利斗:	航 METR 技コ	空工 OLOGY &	OGY 业化 MEAS	& MEASU 深 JII JREMENT ST 量测试式在	大 检 REMENT INST 特区计量 ATION OF CHINA / 开究中心深圳 JREMENT STA	TUTE OF AVI 量 测 试 或 WIATION INDUSTR I计量检测过	C 占 YY 占
	木	交	-	准		证	书		
		(CALI	BRATI	ON C	ERTIFICA 证	TE 书编号	L17AA02992	00000
委托单位	上峰检测认	正有限少) 同			Certifi	cate Number	L17AA02992	.0002
Client 地 址	香港荃灣海			廣塲10	婁D6A	室	and a state of the	No. THE	and
Address 器具名称	声级计/Sou	nd Leve	el M	eters		(0R))**	Annu - Ha	(a) the second	
Description 器具用途	1	Mar H			4 TO	M. APART	A CONCERNING	and the second	
Usage 规格型号	AWA5661	attina'			1 W	and the second	A	No.	est)i
Model/Type 制造单位 Manufacturer	爱华	101.01		11,000 2	N-R	11111 	ALIGNOR CON	Carlos (Laras)	1//
器具编号 Serial No.	301143			inter a		11 contraction	A STATE OF A	14-14-14-14-14-14-14-14-14-14-14-14-14-1	5 100
结 论 Conclusion	见校准结果/	Calibra	tion		1	n vien	AND ADD TO A DOWN		119
conclusion				ALMAN T		准 人 roved by	弱声法沉	J	邵浊沅
	证书专用章)					验员 ecked by	码法沉	,	邵浊沂
					校	准 员 prated by	843		罗成芳
委托日期 Received Date 校准日期 Calibration	2017 2017	年 Year 年 Year	10 10	月 Month 月 Month	23 23	日 Day 日 Day			



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



		校准说明		
	Dir	rections of Calibration		
1.本所(站)是国	家法定计量检定机构,其管理体	、系按照JJF 1069-2012法定计量机构考核	规范、ISO/IEC1702	25:2005和
accordance with	tion is the Service of Legal M	etrological Verification. It has implem Examination of the Service of Legal N	NAME OF TAXABLE PARTY OF TAXABLE PARTY.	
	对被测件有效,所出具的数据均		manufa ta tha nat	tional as
	e only to the items specified. mary standards of measurem	All data issued by the certificate are t ent.	raceable to the hal	uonai or
	许可,不得部分复印此证书内容			
		out the written approval of the institu	te/station.	
4.参照技术依据(Reference documents for the	calibration) :		
参展116 188-200)2《声级计检定规程》《V.R.of	Sound Lovel Meters		
参照110 100-200	2 《 户 级[[1]型] [2] 《V.K.OI	sound Level Wietersy		
5.校准协点及环境	条件 (Place and environment	al conditions of the calibration) :		
地点 (Place)	att () are and entirement	温度 (Temperature)	相对湿度 (Relati	ve Humidity
本所/Lab		22.0 °C		%
6.本次校准所使用	的主要计量标准装置信息(Majo	or standard devices used in the calibr	ation):	10
计量标准名称	测量范围	不确定度或最大允差 或准确度等级	证书编号	有效期
Description	Range	Uncertainty of Measurement or Maximum Permissible Errors	Certificate No.	Due Date
1000000		Moximum remissible Errors	BUT I IN	
7.本次校准所使用	約主要计量标准器且信息(Maid	or standards of measurement used in	the calibration) :	An assess
	A	不确定度或最大允差		
器具名称	编号/型号	或准确度等级	证书编号	有效期
Description	Serial No./Model	Uncertainty of Measurement or Maximum Permissible Errors	Certificate No.	Due Date
可变阻抗衰减器	2300060/984A	U=0.22dB (k=2)	WX17000302209	2018.03.3
	US34020710/33120A	频幅特性:0.20dB,频率:U _{rel} =1E- 7(k=2)	WWS201700237	2018.04.04
函数信号发生器	089867/AWA5810D	± 0.2 dB ; ± 0.5 dB	SSD201700243	2018.01.0
函数信号发生器 测量放大器	A REAL PROPERTY AND A REAL	A DESCRIPTION OF A DESC	SSD201606162	2017.11.13
	2172118/4190	U=0.3 dB (k=2)		
測量放大器	2172118/4190 2292007/4231	U=0.3 dB (k=2) 1级	SSD201606161	2017.11.13



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



the second		ist sh	证书编号:L17AA02992000
	校》	准结果	
	Result o	f Calibration	
	and function	un chask · 正始/Dece	
1、外观及功能正常性检查/Appe		on check:正舟/Pass	and the second
2、声级计指示声级/Level Calibr			
校准前示值/Indication before C			
校准后示值/Indication After Ad			
3、頻率计权/Frequency weight	the manufacture of	A1140	
标称频率	允许下限	A计权	允许上限
Nominal frequency	Lower Limit	A-weighting	Upper Limit
(Hz)	(dB)	(dB)	(dB)
31.5	-42.9	-39.5	-35.9
63	-28.7	-25.4	-23.7
125	-18.1	-16.3	-14.1
250	-10.5	-8.7	-6.7
500	-5.1	-3.5	-1.3
1000 (ref.)	-1.4	0.0	+1.4
2000	-1.4	+1.1	+3.8
4000	-2.5	+1.8	+4.6
标称频率	允许下限	C计权	允许上限
Nominal frequency	Lower Limit	C-weighting	Upper Limit
(Hz)	(dB)	(dB)	(dB)
31.5	-6.5	-3.8	+0.5
63	-3.3	-2.7	+1.7
125	-2.2	-1.5	+1.8
250	-1.9	-0.5	+1.9
500	-1.9	-0.3	+1.9
1000 (ref.)	-1.4	0.0	+1.4
2000	-2.8	+0.8	+2.4
4000	-4.4	+1.9	+2.8



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Ø

中抗工业



证书编号:L17AA029920002

4、级线性(参考频率 1kHz)/Level linearity error(Reference frequency 1kHz) :

4.1、级程变化误差 (参考频率: 1000Hz): A计权/A-weighting

深圳中航技术检测所中国航空工业深圳特区计量测试站

Level Change Error (Reference frequency:1000Hz)

标称值	允许下限	误差	允许上限
Nominal Value	Lower Limit	Error	Upper Limit
(dB)	(dB)	(dB)	(dB)
40	-1.0	-0.3	+1.0
50	-1.0	-0.3	+1.0
60	-1.0	-0.2	+1.0
70	-1.0	+0.2	+1.0
80	-1.0	-0.1	+1.0
90 (ref.)		0.0	
100	-1.0	0.0	+1.0

5、本机噪声/Residual noise:

A计权/A-weighting: _______dB;

Δ6、单个猝发音响应 (A计权) /Tone burst response (A-weighting)

单个猝发音持续时间	猝发	音响应(dB)/Tone b	urst response (d	B)
(ms) /Single tone burst Last time (ms)	L _{AFmax} -L _A	允许范围 /Conclusion	L _{ASmax} ~L _A	允许范围 /Conclusion
500	-0.3	+0.7~-0.9	-3.7	-3.3~-4.9
200	-0.6	-0.2 ~ -1.8	-7.5	-6.6 ~ -8.2
50	-3.9	-3.5 ~ -6.1	-12.5	-11.8 ~ -14.4
10	-10.6	-9.8 ~ -12.4	-20.9	-18.7 ~ -22.3

Δ7、重复猝发音响应(A计权)/Response to repeated Toneburst (A-weighting)

Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

	单个猝发音持续时间 (ms)/Sinale tone	相邻单个猝发音持续时间(ms)	猝发音响应(dB)/Tone burst response(dB)
Sec. State			第4页共5页 Page 4 of 5

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com






Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

中联工业	中国航空工业深圳特国防科技工业第一计量测试研究	区 计 量 测 试 站 四心深圳针最检测站	证书编号:L17	AA029920002
	burst Last time (ms)	acent single tone ourst last (ms)	L _{AEqT} -L _A	允许范围 /Conclusic
	500	2000	-7.6	-6.2 ~ -7.8
	200	800	-7.5	-6.2 ~ -7.8
	50	200	-6.8	-5.7 ~ -8.3
	10	40	-6,5	-5.7 ~ -8.3
附注	: 。关于测量结果不确定度的说	明/Directions of uncertainty	in the calibration :	
	1.依据文件/According to: JJ	IF1059.1-2012测量不确定度语	定与表示	
	JJF1059.1-2012 Evaluation a	and Expression of Uncertain	ty in Measurement ;	
	2.本次测量结果的扩展不确定((k=2)	度/Expanded uncertainty of i	measured results:U=0.4	1dB ~ 1.0dB
	。技术要求参照JJG 188-2002	/MPE according to JJG 188-	2002 ;	
	∆°参考IEC61672-1-2002标》	佳/Reference standard:IEC61	672-1-2002 ;	
	带 "Δ*项目表示未获得CNASi	认可/*Δ* expressed unattaine	ed CNAS accept	
	。建议下次送校日期/Due to c	late : 2018-10-22		
		以下空白/End of data		







委托单位 上峰检测认证有限公司 地址 上峰检测认证有限公司 地址 香港荃灣海盛路3號TML廣塲10樓D6A室 器具名称 声校准器/Sound calibrator 器具用途 / 现格型号 ND9	29920001
证书编号 Certificate Number L17AA0 委托单位 Client 上峰检测认证有限公司 地址 香港荃灣海盛路3號TML廣塲10樓D6A室 器具名称 Description 声校准器/Sound calibrator 器具用途 Usage / 规格型号 ND9	29920001
委托单位 Client 上峰检测认证有限公司 地址 Address 香港荃灣海盛路3號TML廣塲10樓D6A室 器具名称 Description 声校准器/Sound calibrator 器具用途 Usage / 规格型号 ND9	
地 Address 器具名称 Description 器具用途 Usage 规格型号	- Million to -
器 具 名 称 Description 器 具 用 途 Usage 规 格 型 号	
器具用途 Usage	-
规格型号 ND9	syntax.
Model/Type Nos	and a subscription
制造单位 Manufacturer 广州兰泰仪器有限公司	endy and
器具编号 Serial No. 507258	
结论 Conclusion	IN CARLE
批准人 码子法况 Approved by	邵浊沂
(证书专用章) 核验员 码子 水 沉 Checked by	邵迪沂
校准员 Calibrated by	罗成判
委托日期 2017 年 10 月 23 日 Received Date Year Month Day	
校准日期 2017 年 10 月 23 日 回路型 Calibration Year Month Day	



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



		校准说明		
	Dir	ections of Calibration		
1.本所(站)是国 CNAS相关要求运行		系按照JIF 1069-2012法定计量机构考核	规范. ISO/IEC1702	25:2005和
accordance with		etrological Verification. It has implem Examination of the Service of Legal M		
	对被测件有效,所出具的数据均	可溯源到国家或国际计量基准,		
		All data issued by the certificate are to	raceable to the nat	tional or
	nary standards of measureme 午可,不得部分复印此证书内容			
Here and the second second		。 out the written approval of the institu	te/station.	
	Reference documents for the		12/10/11/201	
参照JJG 176-200	5《声校准器检定规程》《V.R.d	f Sound Calibrators)		
5.校准地点及环境经	条件 (Place and environment	al conditions of the calibration) :		
也点 (Place)	Same And an And And And	温度 (Temperature)	相對湿度 (Relati	ve Humidity
本所/Lab		22.2 °C	60)%
5.本次校准所使用的	的主要计量标准装置信息 (Majo	or standard devices used in the calibra	ation):	SUNNER DE LA
		不确定度或最大允差	WE ASIA D	-
计量标准名称	测量范围	或准确度等级	证书编号 Certificate No.	有效期 Due Date
Description	Range	Uncertainty of Measurement or Maximum Permissible Errors	Certificate No.	Due Date
	A ANTARA		TOWN DEPOS	
木次核准時時間	り 主要注意 伝達 照見 信息(Main	r standards of measurement used in	the calibration)	MAX.
-T-VILOPPINEODH	2.2.3c ri menoeranisettano (anolo	不确定度或最大允差		In the second
器具名称	编号/型号	或准确度等级	证书编号	有效期
Description	Serial No./Model	Uncertainty of Measurement or	Certificate No.	Due Date
	A second second second	Maximum Permissible Errors	s-m(69)/2"	
測量放大器	089867/AWA5810D	± 0.2 dB ; ± 0.5 dB	SSD201700243	2018.01.09
	2172118/4190	U=0.3 dB (k=2)	SSD201606162	2017.11.13
标准传声器	CONTRACTOR OF STREET	1级	SSD201606161	2017.11.13
标准传声器	2292007/4231			0132607
Estant of a	2292007/4231	And the second second		
	2292007/4231	and started		
Estant of a	2292007/4231			
Estant of a	2292007/4231	and an and a second		
Estant of a	2292007/4231	and the second s		
	2292007/4231			



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



	校准	结果	
	Result of	Calibration	
1	外观及功能正常性检查:	正常	
	Visibility and function inspec	tion : Pass.	
2	声压级校准/Sound pressure le	evel calibration :	
	规定声压级/Provisions of sound pressure level (dB)	测量声压级/Measurement of sour pressure level(dB)	声压级差的绝对值/ d The absolute value o sound pressure leve difference(dB)
	114	114.4	0.4
	94	94.3	0.3
3	频率校准/Frequency calibratio	m :	
	规定频率(Hz)	測量频率(Hz)	频率误差(%)
	assigned frequency	assigned frequency	frequency error
	1000	1000.09	0.0
4	失真度校准/Distortion calibrat	ion :	star and
	规定颜率(Hz)	规定声压级/Provisions of sound	总失值(%)
	assigned frequency	pressure level (dB)	Distortion
	1000	94	0.03
	1000	114	0.09
附注:		Constantine Constant	
Rema	rk Directions of uncertainty in m	easurement :	
	1.依据文件: JJF1059.1-2012 汉		
	Ref.document : JJF1059.1-20	12 Evaluation and Expression of une	certainty in measurement
	2.本次测量结果的扩展不确定度	Constant Stands	
	Expanded uncertainty of the r		
		_{el} =0.1%;失真: <i>U</i> _{rel} =0.5%;(<i>k</i> =2	
	◇ 建议下次送校日期/Due to dat	te : 2018-10-22	
		空白/End of Data	



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Appendix E Impact Monitoring Data of Noise

Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area

Da	ata of Monitoring												3/5/2	2018											
	nitoring Location		NSR1 (EP)																						
Descri	ption of the Location		Sir Ellis Kadoone See School																						
Sou	and Level Method		Sound level meter : AWA5661 SN304042																						
(Mo	del and Serial No.)		Calibrator: ND9 SIN507258																						
Weather	Status		Sunny																						
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	ର୍ଟ(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Monitoring	Finish	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30	19:00
	L10 dB(A)	64.5	65.2	65.4	65.7	66.5	66.9	67.2	66.3	67.0	67.7	66.9	66.5	66.4	65.8	65.9	66.3	66.5	66.7	66.1	67.5	66.8	65.4	65.9	65.3
	L90 dB(A)	55.8	56.4	56.1	57.3	58.4	58.9	60.2	60.7	61.9	61.3	60.8	61.2	61.1	60.5	59.7	60.3	61.3	60.6	59.9	61.8	60.2	59.5	58.7	58.2
Measured Noise	Leq dB(A)	62.7	63.1	63.3	63.8	64.4	64.5	65.1	64.6	65.0	65.4	64.7	64.9	64.2	63.9	63.7	64.0	64.4	64.0	64.2	65.3	64.7	63.1	63.5	63.2
Level (dB(A))	L10 (Average)			-									66	.3											
	L90 (Average)												59.	.9											
	Leq (30 min)												64.	.2											
Noise Li	mit Level, Leq, (dB(A))										70	dB(A) for s	chool/65 d	B(A) durin	g examinat	ion									
Site C	onstruction Activities												Backfillir	ng Works											
Other Noise S	ources During Measurement											Hu	nan Activiti	es and Veh	icle										

EEM

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	after	26/5/2018

Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation

D	ata of Monitoring												3/5/.	2018											
Mo	onitoring Location		NSR7 (EP)																						
Descr	iption of the Location		Fu Yun House																						
Sound Level N	fethod (Model and Serial No.)		Sound level meter : AWA5661 \$\N301143 Calibrator: ND9 \$\N507258																						
Weather	Status												Su												
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Monitoring	Finish	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30	19:00
	L10 dB(A)	71.3	71.7	72.8	72.6	70.4	71.9	73.5	72.6	72.9	73.7	72.4	72.6	74.4	73.1	72.2	71.3	71.8	72.4	74.3	73.7	72.1	71.6	71.4	72.2
	L90 dB(A)	63.1	63.5	64.3	64.1	63.8	63.2	65.4	64.4	63.9	64.6	63.7	63.6	65.5	65.0	64.3	63.7	63.2	64.4	66.8	65.9	65.3	63.4	63.2	64.3
Measured Noise	Leq dB(A)	69.5	69.3	70.1	70.3	68.7	69.3	71.1	70.4	70.8	71.3	70.5	70.8	72.1	71.8	70.3	69.7	69.2	70.7	72.5	71.6	70.3	69.7	69.3	70.4
Level (dB(A))	L10 (Average)												72	.6											
	L90 (Average)												64	.4											
	Leq (30 min)												70	.5											
Noise Li	mit Level, Leq, (dB(A))												75d	B(A)											
Site C	onstruction Activities												Backfilli	ng Works											
Other Noise S	Sources During Measurement											Hu	nan Activit	ies and Veh	icle										

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	atta	26/5/2018

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area

Da	ata of Monitoring												9/5/	2018											
Mo	onitoring Location												NSR	(EP)											
Descri	iption of the Location											Sir	Ellis Kadoo	one Sec Sch	ool										
Sou	und Level Method											Sound lev	el meter : A	WA5661 S	N304042										
(Mo	del and Serial No.)											Ca	librator: NI	9 S/N5072	58										
Weather	Status												Clo	udy											
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)										
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Monitoring	ng Finish 7:30 8:00 8:30 9:00 9:30 10:00 10:30 11:00 11:30 12:00 12:30 13:00 14:00 14:30 15:00 15:30 16:00 16:30 17:00 17:30 17:00 17:30 16:00 16:00 17:00 1												18:00	18:30	19:00										
Monitoring Finish 7:30 8:00 8:30 9:00 9:30 10:00 11:30 12:30 13:30 14:30 15:30 15:30 16:30 <t< td=""><td>65.7</td><td>65.4</td></t<>											65.7	65.4													
	L90 dB(A)	57.2	60.4	61.1	59.5	58.6	61.3	61.8	61.5	62.2	62.4	62.7	61.9	60.5	60.7	60.9	61.6	61.3	60.5	60.6	59.8	58.6	58.7	58.3	58.6
Measured Noise	Leq dB(A)	63.5	64.2	64.0	63.9	63.7	64.4	64.6	64.9	65.5	65.0	65.5	64.8	64.1	64.3	64.7	65.3	65.1	64.7	64.0	64.3	63.9	63.6	63.1	63.7
Level (dB(A))	L10 (Average)												66	.5											
	L90 (Average)												60	.7											
	Leq (30 min)												64	.4											
Noise Li	mit Level, Leq, (dB(A))										70	dB(A) for s	chool / 65 c	B(A) during	g examinat	ion									
Site C	onstruction Activities												Backfilli	ng Works											
Other Noise S	Sources During Measurement											Hu	nan Activit	ies and Veh	icle										

FEF

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	10th	26/5/2018

Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation

Da	ata of Monitoring												9/5/2	2018											
Mc	onitoring Location												NSR7	(EP)											
Descri	ption of the Location												Fu Yun	House											
Sound Level M	lethod (Model and Serial No.)												el meter : A librator: NE												
Weather	Status												Clo	udy											
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)											
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Monitoring	Finish	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30	19:00
	L10 dB(A)	70.4	71.3	72.7	72.5	72.4	73.6	72.9	74.7	74.6	73.5	73.9	72.8	72.2	72.3	71.1	72.1	70.4	71.5	73.3	72.0	72.1	71.4	71.9	71.3
	L90 dB(A)	64.1	65.2	66.5	66.7	66.3	67.4	66.9	67.8	67.3	66.2	66.0	67.2	66.1	65.1	64.7	65.3	64.7	65.3	64.8	64.1	64.3	63.5	63.2	63.7
Measured Noise	Leq dB(A)	68.6	69.6	70.1	70.3	70.0	71.4	70.8	72.5	72.2	71.4	71.6	70.5	70.8	70.4	69.9	70.6	68.8	69.3	71.4	70.7	70.8	69.3	69.8	69.3
Level (dB(A))	L10 (Average)												72	.5											
	L90 (Average)												65	.7											
	Leq (30 min)												70	.5											
Noise Li	mit Level, Leq, (dB(A))												75dI	3(A)											
Site Co	onstruction Activities												Backfillir	ig Works											
Other Noise S	ources During Measurement											Hu	nan Activiti	es and Veh	icle										

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	10th	26/5/2018

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area

Da	ata of Monitoring												15/5/	2018											
Mc	onitoring Location												NSR1	(EP)											
Descri	ption of the Location											Sir	Ellis Kadoc	ne Sec Sch	ool										
Sou	und Level Method											Sound lev	el meter : A	WA5661 S	/N304042										
(Mo	del and Serial No.)											Ca	librator: NE	9 S/N5072	58										
Weather	Status												Sur	iny											
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)										
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Monitoring	Finish	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30	19:00
	L10 dB(A)	65.6	66.2	66.3	66.6	67.4	67.2	67.9	67.3	67.1	66.3	66.5	67.1	67.4	66.8	66.9	66.2	65.7	65.3	66.1	65.9	65.5	65.4	65.7	65.2
	L90 dB(A)	58.4	57.9	58.3	60.2	61.4	61.6	61.9	62.2	60.7	60.9	61.1	62.0	61.7	60.5	61.1	60.3	59.2	58.7	60.1	58.6	58.4	58.9	57.5	58.2
Measured Noise	Leg dB(A)	63.8	63.9	64.1	64.5	65.3	65.0	65.7	65.2	64.9	64.7	64.4	65.0	65.3	64.7	64.5	64.1	63.9	63.8	64.2	63.7	63.5	63.3	63.8	63.1
Level (dB(A))	L10 (Average)			-									66	5											
	L90 (Average)												60	2											
	Leq (30 min)												64	4											
Noise Li	mit Level, Leq, (dB(A))										70	dB(A) for s	chool / 65 d	B(A) during	g examinat	on									
Site C	onstruction Activities												Backfillir	ig Works											
Other Noise S	ources During Measurement											Hui	nan Activiti	es and Veh	icle										

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	12this	26/5/2018

Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation

Da	ata of Monitoring												15/5/	2018											
	onitoring Location												NSR												
Descri	iption of the Location												Fu Yun	House											
Sound Level M	fethod (Model and Serial No.)												el meter : A librator: NI												
Weather	Status												Sui	iny											
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)											
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
											18:00	18:30	19:00												
	L10 dB(A)	72.1	70.8	72.3	72.4	72.5	71.7	71.6	72.3	73.1	73.5	74.4	74.7	73.8	74.9	72.6	72.7	73.4	74.6	73.8	73.4	72.9	72.6	71.7	71.8
	L90 dB(A)	62.9	62.8	63.0	63.5	63.8	64.1	64.0	64.8	65.5	65.8	66.2	66.3	65.7	66.8	65.2	65.6	66.1	67.3	66.9	65.8	65.0	64.9	63.7	63.5
Measured Noise	Leq dB(A)	69.0	68.7	69.2	70.0	70.1	69.4	69.2	70.8	71.4	71.6	72.5	72.2	71.1	72.3	70.7	70.9	71.7	72.8	71.4	71.0	70.4	70.3	69.6	69.2
Level (dB(A))	L10 (Average)			-	-								73	0											
	L90 (Average)												65	2											
	Leq (30 min)												70	8											
Noise Li	mit Level, Leq, (dB(A))												75d1	3(A)											
Site C	onstruction Activities												Backfilli	ig Works											
Other Noise S	Sources During Measurement											Hui	nan Activit	es and Veh	icle										

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	10 Fri	26/5/2018

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area

Da	ata of Monitoring												21/5/	2018											
	onitoring Location												NSRI												
Descri	ption of the Location											Sir	Ellis Kadoo	one Sec Sch	ool										
	and Level Method											Sound lev	el meter : A	WA5661 S	N304042										
(Mo	del and Serial No.)											Ca	librator: NE	9 S/N5072	58										
Weather	Status												Fi	ne											
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)										
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Monitoring Finish 7:30 8:00 8:30 9:00 9:30 10:00 11:30 12:00 12:30 13:00 14:30 14:30 15:00 15:30 16:00 16:30 11:30											17:00	17:30	18:00	18:30	19:00										
	L10 dB(A)	65.2	66.6	66.8	67.4	67.6	66.9	66.2	66.3	65.4	65.8	66.5	66.6	65.9	65.8	66.2	67.1	67.4	67.2	66.3	66.5	65.7	65.9	65.3	65.4
	L90 dB(A)	58.2	58.3	58.4	59.2	59.4	60.2	60.5	60.7	59.2	59.8	60.5	60.8	59.2	59.8	60.2	61.3	61.5	61.7	60.5	60.2	59.2	59.1	59.7	59.4
Measured Noise	Leq dB(A)	63.3	64.2	64.5	65.1	65.3	64.7	64.8	64.1	63.8	63.9	64.2	64.4	63.5	63.7	64.3	65.0	65.2	65.4	64.7	64.4	63.2	63.8	63.1	63.5
Level (dB(A))	L10 (Average)									-			66	.4											
	L90 (Average)												60	.0											
	Leq (30 min)												64	.3											
Noise Lii	mit Level, Leq, (dB(A))										70	dB(A) for s	chool / 65 d	B(A) durin	g examinati	ion									
Site Co	onstruction Activities												Backfillir	ng Works											
Other Noise S	ources During Measurement								_			Hui	nan Activiti	ies and Veh	icle				_						

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	1 the	26/5/2018

Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation

Da	ata of Monitoring												21/5/	2018											
	onitoring Location												NSR7												
	ption of the Location												Fu Yun	House											
	lethod (Model and Serial No.)												el meter : A librator: NE												
Weather	Status												Fi	ne											
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)											
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Intervi Jain Job Job <thjob< td=""><td>17:00</td><td>17:30</td><td>18:00</td><td>18:30</td><td>19:00</td></thjob<>										17:00	17:30	18:00	18:30	19:00											
	L10 dB(A)	71.6	71.7	72.2	72.5	71.6	72.4	73.3	73.7	74.4	74.6	73.5	74.7	75.6	75.8	74.9	73.2	73.8	72.4	72.5	71.6	71.8	71.9	71.7	71.3
	L90 dB(A)	63.5	63.4	63.8	64.1	63.9	63.3	64.1	64.0	65.3	65.7	65.1	65.8	66.0	65.9	65.7	65.2	65.3	64.8	64.2	63.8	63.4	63.2	63.8	63.1
Measured Noise	Leq dB(A)	69.3	69.7	70.1	70.4	69.3	70.8	71.5	71.9	72.2	72.4	71.3	72.8	73.3	73.0	72.1	71.5	71.8	70.2	70.3	69.4	69.1	69.3	69.4	69.2
Level (dB(A))	L10 (Average)												73	.2						÷		÷			
	L90 (Average)												64	.5											
	Leq (30 min)												71	.1											
Noise Li	mit Level, Leq, (dB(A))												75dI	B(A)											
Site C	onstruction Activities												Backfillir	ig Works											
Other Noise S	ources During Measurement											Hu	man Activiti	es and Veh	icle										

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	12th	26/5/2018

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area

Data of Monitoring 26/5/2018																									
Monitoring Location NSR1 (EP)																		-							
Descri	Sir Ellis Kadoone Sec School																								
So	und Level Method		Sound level meter : AWA5661 S/N304042																						
(Mc	odel and Serial No.)						Calibrator: ND9 SNS07258																		
Weather	Status												Sui	nny											
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Monitoring	Finish	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30	19:00
	L10 dB(A)	65.4	66.1	66.0	65.8	66.6	67.0	67.4	67.3	66.5	66.9	66.3	65.1	65.5	66.4	66.9	66.8	66.4	67.3	67.6	66.2	66.4	65.9	65.3	65.2
	L90 dB(A)	59.2	59.6	59.4	59.8	60.6	61.3	61.4	61.8	60.6	60.7	60.5	59.7	59.3	59.8	60.5	61.1	61.3	62.0	62.2	61.9	61.3	59.9	59.7	59.8
Measured Noise	Leq dB(A)	63.5	63.9	63.8	63.5	64.1	65.2	65.0	65.1	64.4	64.7	64.0	63.2	63.8	63.9	64.1	64.6	64.7	65.0	65.3	64.6	64.0	63.8	63.7	63.5
Level (dB(A))	L10 (Average)	66.4																							
	L90 (Average)												60	.7											
	Leq (30 min)												64	.3											
Noise Li	imit Level, Leq, (dB(A))										70	dB(A) for s	chool / 65 d	B(A) during	g examinati	on									
Site C	onstruction Activities												Backfilli	ng Works											
Other Noise S	Sources During Measurement											Hu	nan Activit	ies and Veh	icle										

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	1 the	26/5/2018

Noise Monitoring Record Sheet

Contract No: SS D505

Contract Title: Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum- Vehicle Depot at Yen Ming Road, West Kowloon Reclamation

D	ata of Monitoring												26/5	2018											·,
	onitoring Location	NSR7 (EP)																							
Descri	ption of the Location	Fu Yun House																							
Sound Level N	fethod (Model and Serial No.)	Sound level meter : AWA5661 S/N301143 Calibrator: ND9 S/N507258																							
Weather	Status												Su	nny											-
Condition	Wind Strength (m/s)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)	<5(E)
Time of	Start	7:00	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30
Monitoring	Finish	7:30	8:00	8:30	9:00	9:30	10:00	10:30	11:00	11:30	12:00	12:30	13:00	13:30	14:00	14:30	15:00	15:30	16:00	16:30	17:00	17:30	18:00	18:30	19:00
	L10 dB(A)	70.1	71.3	72.5	72.9	71.4	71.5	72.7	73.3	73.5	73.4	72.6	72.2	73.3	74.8	74.7	74.5	73.9	72.1	71.4	71.7	71.3	71.8	71.4	71.5
	L90 dB(A)	63.5	63.4	64.4	64.5	63.9	63.8	64.2	65.3	65.7	65.5	64.9	64.8	65.7	66.6	66.9	66.4	65.9	65.3	65.7	65.0	64.8	63.8	63.2	63.4
Measured Noise	Leq dB(A)	68.9	69.2	70.4	70.1	69.5	69.2	70.8	71.4	71.2	71.0	70.9	70.7	71.8	72.2	72.4	72.3	71.8	70.8	69.2	69.3	69.4	69.7	69.0	69.1
Level (dB(A))	L10 (Average)	72.7																							
	L90 (Average)												65	.0											
	Leq (30 min)												70	.6											
Noise Li	mit Level, Leq, (dB(A))												75d	3(A)											
Site C	onstruction Activities												Backfilli	ng Works											
Other Noise Sources During Measurement Human						man Activit	ies and Veh	icle										-							

	Name	Signature	Date
Recorded by	Mary Yiu	2	26/5/2018
Checked by	Calvin Lui	10 Fri	26/5/2018


香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Appendix F Graphical Plot of Leq (30 min)

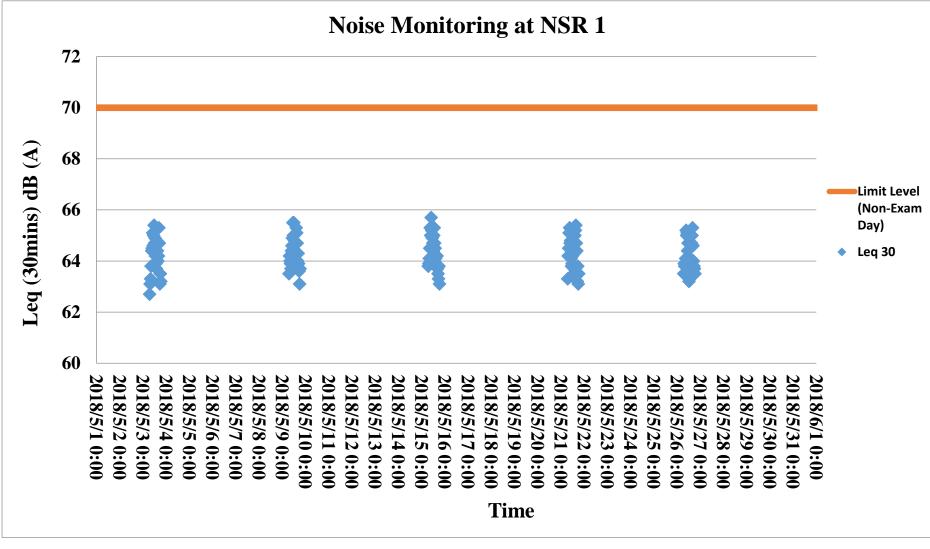


香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



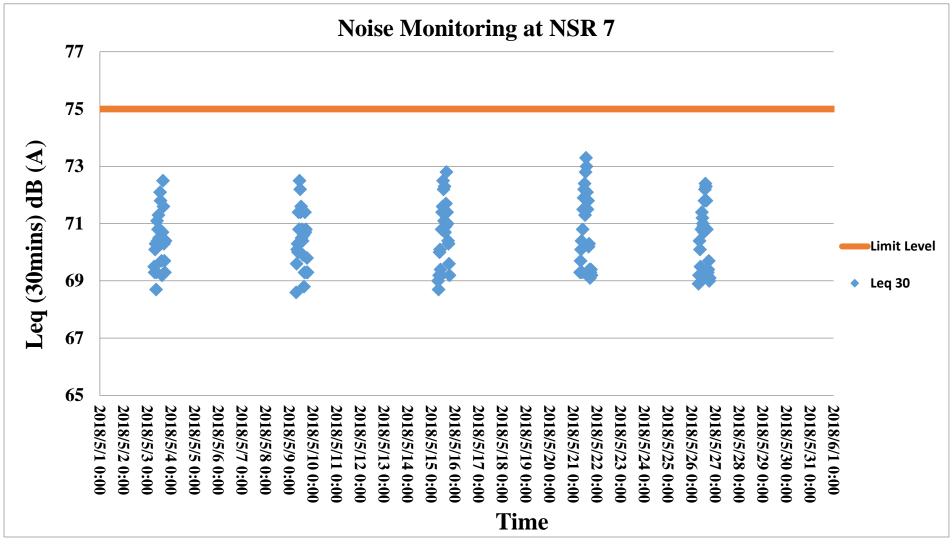

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Appendix G Monitoring Schedule

Impact Monitoring Schedule (May 2018) [i.e. Reporting Period]

						May 2018
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2	3 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	4	5
6	7		9 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900		11	12
13	14	15 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	16	17	18	19
20	21 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	22	23	24	25	26 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900
27	28	29	30	31		

Remarks: IN - Impact Noise Monitoring

NSR 1 -Sir Ellis Kadoorie Secondary School (West Kowloon)

NSR 7 - Fu Cheong Estate Fu Yun House





Impact Monitoring Schedule for future three months [i.e. June, July and August 2018]

Impact Monitoring Schedule (June 2018)

						June 2018
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					1 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	2
3	4	5	6	7 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	0	9
10	11	12	13 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	14	15	16
17	18	19 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	20	21	22	23
24	25 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	26	27	28		30 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900

Remarks: IN – Impact Noise Monitoring

NSR 1 –Sir Ellis Kadoorie Secondary School (West Kowloon)

NSR 7 - Fu Cheong Estate Fu Yun House





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com Impact Monitoring Schedule (July 2018)

						July
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1	2	3	4	-	6 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	7
8	9	10	11	12 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	13	14
15	16		18 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	19	20	21
22	23	24 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	25	26	27	28
29	30 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	31				

Remarks: IN – Impact Noise Monitoring

NSR 1 –Sir Ellis Kadoorie Secondary School (West Kowloon)

NSR 7 - Fu Cheong Estate Fu Yun House



Telemax Environmental and Energy Management Limited Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Impact Monitoring Schedule (August 2018)

						August 2018
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			1	2		4 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900
5	6	7	8	9	10 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	11
12	13	14	15	16 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	17	18
19	20	21	22 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	23	24	25
26	27	28 IN - NSR 1 & NSR 7 NSR 1: 0700 -1900 NSR 7: 0700 -1900	29	30	31	

Remarks: IN – Impact Noise Monitoring

NSR 1 -Sir Ellis Kadoorie Secondary School (West Kowloon)

NSR 7 - Fu Cheong Estate Fu Yun House


Exam – Exam period for NSR -1





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Appendix H Project Layout

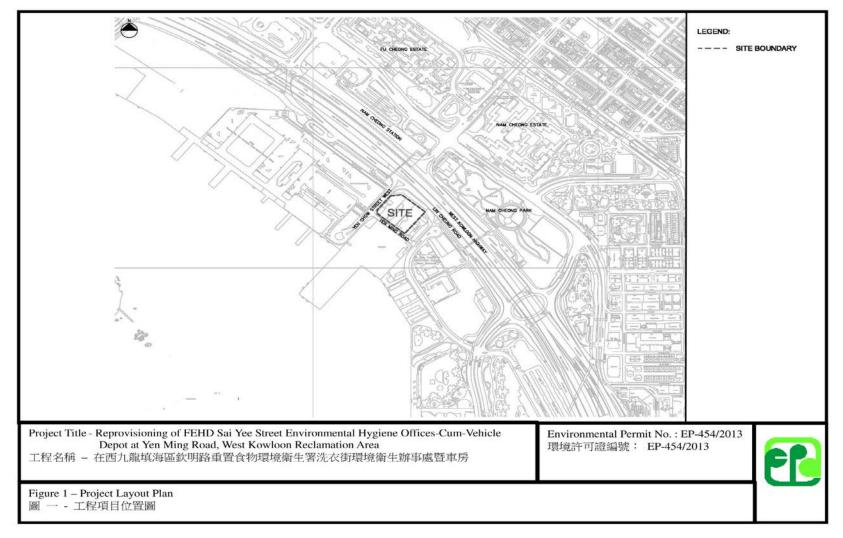






Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Appendix I Location of the Impact Monitoring Locations

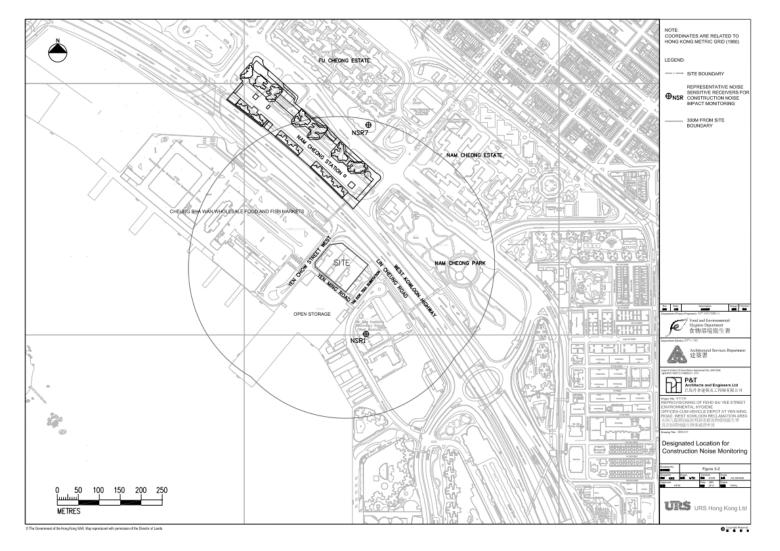



Telemax Environmental and Energy Management Limited Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Appendix J Photo Records of Monitoring

Photo Records of Noise Monitoring in Daytime



NSR 1 - Sir Ellis Kadoorie Secondary School (West Kowloon)



NSR 7 - Fu Cheong Estate Fu Yun House



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Appendix K Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Cumulative statistics for complaints, notifications of summons and successful prosecutions for the Project account for period starting from the date of commencement of construction works (i.e. 29 February 2016) to the end of the reporting month and are summarized in the Table L-1 below.

Reporting Period	Received Date		Cumulative Statistics							
		Complaints	Notifications of summons	Successful prosecutions	Туре	Status				
This reporting month	N/A	0	0	0	N/A	N/A				
From 29 February 2016 to end of the reporting month		2	0	0						

Table L1 Statistics for complaints, notifications of summons and successful prosecutions



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Appendix L Monthly Waste Flow Table

MA P3 ConstructionWaste Management Plan

MA 11 Construciton Waste Reduction

Project: FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot, Yen Ming Road, West Kowloon Reclamation Area Record by: China Road and Bridge Corporation Year of Record: 2018

Monthly Waste Flow Table

DD.MM.YY	Total Quantity	Total Quantity		A	Actual Qua	ntities of Inert C	&D Mater	als Genera	ated Monthl	у		Actu	ual Quantitie	s of C&D M	aterials Ge	nerated Mo	nthly
	Generated	Generated (Excluded		avated Mater					ed Material	-	r	Metals (steel bar /	Metals (aluminum	Paper / cardboard	Plastics	Chemical waste	Other, e.g. general
		Excavated Material)	Disposed in Public Fill	Disposed in Sorting Facilities	Others (e.g Reused in the Contract / Other Projects)	Broken Concrete or Construction Waste Collected by Recycled Company	Reused in the Contract	Reused in other Projects	Disposed in Public Fill	Disposed in Landfill	Disposed in Sorting Facilities	(ited bar / metal strip)	can) ⁽¹⁾	packaging ⁽¹⁾		(wasted lubricant oil/oil container)	refuse
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)
	a1	a2	b	b	b	С	d	е	f	g	h	i	j	k	1	m	n
2-May-18	6.23	6.23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	6.23
3-May-18	8.63	8.63	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.63
5-May-18	9.28	9.28	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	9.28
7-May-18	25.15	8.83	16.32	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.83
8-May-18	13.40	13.40	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.40
9-May-18	23.36	16.78	6.58	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.78
10-May-18	23.13	8.40	14.73	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.40
11-May-18	26.90	11.99	14.91	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.99
12-May-18	33.26	11.54	21.72	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.54
14-May-18	12.68	12.68	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.68
15-May-18	11.28	11.28	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.28
16-May-18	23.07	7.83	15.24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	7.83
17-May-18	8.62	8.62	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.62
18-May-18	20.56	4.40	16.16	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.40
19-May-18	45.52	30.28	15.24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	30.28
24-May-18	4.51	4.51	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.51
25-May-18	17.48	17.48	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.48
26-May-18	4.45	4.45	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.45
28-May-18	4.38	4.38	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.38
29-May-18	17.59	13.66	3.93	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	13.66
30-May-18	22.83	22.83	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.83
31-May-18	19.70	19.70	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	19.70
Total	382.01	257.18	124.83	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	257.18

Total C&D waste generated Total C&D waste generated (excluded excavated materials) Total recycled C&D waste % of recycled C&D waste for BEAM Plus MA11 382.01 tonnes a1=b+c+d+e+f+g+h+i+j+k+l+m+n

257.18 tonne a2=c+d+e+f+g+h+i+j+k+l+m+n

- 0.00 tonne a3=c+d+e+i+j+k+l
- 0.00 % a4=a3/a2 x 100%

Notes: (1) metal, paper & plastic were collected by recycler

(2) The performance target of waste recycling are specified in the Contractt.

(3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 (4) Plastics refer to plastic bottles/ containers, plastic/foam from packaging material.
 (5) Broken concrete for recycling into aggregates.
 (6) Excavated materials/waste will <u>NOT</u> be considered as part of construction waste. It should be excluded in the calculation.

(7) Disposal of inert waste to public fill or sorting facilities will NOT be considered as recycled waste.



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Notes



MA P3 ConstructionWaste Management Plan

MA 11 Construciton Waste Reduction

 Project:
 FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot, Yen Ming Road, West Kowloon Reclamation Area

 Record by:
 China Road and Bridge Corporation

 Year of Record:
 2018

Overall Summary Waste Flow Table

DD.MM.YY	Total Quantity	Total Quantity		A	Actual Qua	ntities of Inert C	&D Mater	ials Genera	ated Month	y		Act	ual Quantitie	s of C&D M	aterials Ge	enerated Mo	nthly
	Generated	Generated (Excluded	Exca	Excavated Materials Non-excavated Materials							Metals	Metals	Paper /	Plastics	Chemical	Other, e.g.	
		(Excluded Excavated	Disposed in	Disposed in	Others (e.a	Broken Concrete	Reused in	Reused in	Disposed in	Disposed in	Disposed in	(steel bar /	(aluminum	cardboard	(1) & (4)	waste	general
		Material)	Public Fill	Sorting	Reused in	or Construction	the	other	Public Fill	Landfill	Sorting	metal strip)	can) (1)	packaging (1)		(wasted lubricant	refuse
				Facilities	the	Waste Collected	Contract	Projects			Facilities					oil/oil	
					Contract / Other	by Recycled Company										container)	
					Projects)	Company											
					.,,												
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)
	a1	a2	b	b	b	с	d	е	f	g	h	i	j	k	1	m	n
Mar-16	36.48	4.58	31.90	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2.58	0.00	0.00	0.00	0.00	2.00
Apr-16	9.20	9.20	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	9.20
May-16	4.60	4.60	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.60
Jun-16	4.20	4.20	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.20
Jul-16	3.80	3.80	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	3.80
Aug-16	109.80	0.50	109.30	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.50
Sep-16 Oct-16	659.70	8.10	651.60 1279.40	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	8.10
	1280.90	1.50		0.00	0.00	0.00			0.00	0.00	0.00	0.00			0.00	0.00	1.50 4.30
Nov-16	1463.50	4.30 5.22	1459.20	0.00	0.00	0.00	0.00	0.00	0.00		0.00		0.00	0.00	0.00	0.00	
Dec-16	2590.32	5.22	2585.10	0.00	0.00		0.00			0.00		1.72	0.00	0.00		0.00	3.50
Jan-17 Feb-17	765.30 5265.80	4.50	747.40 5261.30	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.90 4.50
Mar-17	5265.80 6161.20	4.50	6156.20	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.50
Apr-17	2230.12	24.12	2206.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	12.92	0.00	0.00	0.00	0.00	5.00
May-17	1592.44	24.12	1565.70	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	4.94	0.00	0.00	0.00	0.00	21.80
Jun-17	949.60	39.20	910.40	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	39.20
Jul-17	1081.92	31.88	1050.04	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	31.88
Aug-17	52.82	52.82	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	52.82
Sep-17	90.88	85.47	5.41	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	85.47
Oct-17	202.80	55.98	146.82	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	55.98
Nov-17	76.74	76.74	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	76.74
Dec-17	201.74	81.31	120.43	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	81.31
Jan-18	286.71	74.17	212.54	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	74.17
Feb-18	96.60	72.29	24.31	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	72.29
Mar-18	254.50	132.29	122.21	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	132.29
Apr-18	163.58	123.87	39.71	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	123.87
May-18	382.01	257.18	124.83	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	257.18
Total	25471.67	826.41	24645.26	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.16	0.00	0.00	0.00	0.00	804.25

Total C&D waste generated Total C&D waste generated (excluded excavated materials) Total recycled C&D waste % of recycled C&D waste for BEAM Plus MA11
 25471.67
 tonnes
 a1=b+c+d+e+f+g+h+i+j+k+l+m+n

 826.41
 tonne
 a2=c+d+e+f+g+h+i+j+k+l+m+n

 22.16
 tonne
 a3=c+d+e+i+j+k+l

 2.68%
 a4=a3/a2 x 100%
 b100%

(1) metal, paper & plastic were collected by recycler
 (2) The performance target of waste recycling are specified in the Contractt.
 (3) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
 (4) Plastics refer to plastic bottles/ containers, plastic/ foam from packaging material.
 (5) Broken concrete for recycling into aggregates.
 (6) Excaveted materials/waste will <u>NOT</u> be considered as part of construction waste. It should be excluded in the calculation.
 (7) Disposal of inert waste to public fill or sorting facilities will <u>NOT</u> be considered as recycled waste.



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Appendix M Environmental Licenses / Permits

(a) Environmental Permit

Environmental Permit No. EP-454/2013 環境許可證編號EP-454/2013

ENVIRONMENTAL IMPACT ASSESSMENT ORDINANCE (CHAPTER 499) Section 10

環境影響評估條例 (第499章) 第10條

ENVIRONMENTAL PERMIT TO CONSTRUCT AND OPERATE

A DESIGNATED PROJECT

建造及營辦指定工程項目的環境許可證

PART A (MAIN PERMIT)

A部(許可證主要部分)

Pursuant to Section 10 of the Environmental Impact Assessment Ordinance (EIAO), the Director of Environmental Protection (the Director) grants this environmental permit to the <u>Food and Environmental</u> <u>Hygiene Department</u> (hereinafter referred to as the "Permit Holder") to construct and operate the designated project described in <u>Part B</u> subject to the conditions specified in <u>Part C</u>. The issue of this environmental permit is based on the documents, approvals or permissions described below :-

根據《環境影響評估條例》(環評條例)第10條的規定,環境保護署署長(署長)將本環境許可證批予<u>食物</u> 環境衛生署(下稱許可證持有人)以建造及營辦<u>B部</u>所說明的指定工程項目,但須遵守<u>C部</u>所列明的條件。 本環境許可證是依據下列文件、批准或許可而簽發:-

Application No. 申請書編號	AEP-454/2013
Document in the Register 登記冊上文件	 (1) Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area (Register No.: AEIAR-177/2013) Environmental Impact Assessment Report (June 2013) [Hereinafter referred to as the "EIA Report"] Environmental Monitoring and Audit Manual (June 2013) [Hereinafter referred to as the "EM&A Manual"] Executive Summary (June 2013)
	在西九龍填海區欽明路重置食物環境衞生署洗衣街環境衞生辦 事處暨車房 (登記冊編號: AEIAR-177/2013) - 環境影響評估報告 (2013年6月) [下稱「環評報告」] - 環境監察審核手冊 (2013年6月) [下稱「環監手冊」] - 行政摘要 (2013年6月)
	(2) The Director's letter of approval of the EIA report dated 12 November 2013 referenced (69) in EP 2/K20/A20 Pt.2
	署長於2013年11月12日發出批准環評報告的信件,檔案編號: (69) in EP 2/K20/A20 Pt.2
	(3) Application for an Environmental Permit submitted by the Permit Holder on 24 June 2013 (Application No.: AEP-454/2013)
	許可證持有人於2013年6月24日提交的環境許可證申請(申請書



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



	編號: AEP-454/2013)
-	
-	
- 12 November 2013	
2013年11月12日	
Date 日期	 (Ken Y.K. Wong) Principal Environmental Protection Officer for Director of Environmental Protection 環境保護署署長 (首席環境保護主任 黃羅光代行)

PART B (DESCRIPTION OF DESIGNATED PROJECT)

B部(指定工程項目的說明)

Hereunder is the description of the designated project mentioned in Part A of this environmental permit (hereinafter referred to as the "Permit"):-

下列為本環境許可證(下稱"許可證")A部所提及的指定工程項目的說明:

Title of Designated Project(s) 指定工程項目的名稱	Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices- cum-vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area [This designated project is hereinafter referred to as "the Project"] 在西九龍填海區欽明路重置食物環境衞生署洗衣街環境衞生辦事處暨車 房 [這指定工程項目下稱"工程項目"]
Nature of Designated Project(s) 指定工程項目的性質	A transport depot located less than 200m from the nearest boundary of an existing or planned residential area / educational institution 運輸車廠的位置距離一個現有的或計劃中的住宅區或教育機 構的最近界線少於200 米
Location of Designated Project(s) 指定工程項目的地點	The Project is located at Yen Ming Road, West Kowloon Reclamation Area. The location of this Project is shown in <u>Figure 1</u> attached to this Permit. 工程項目位於西九龍填海區欽明路。工程項目的位置見載於本許可證夾 附的 <u>圖1</u> 。
Scale and Scope of Designated Project(s) 指定工程項目的規模和範圍	The project is to construct and operate a five-storey building comprising various facilities for vehicle washing and repair operation, parking of vehicles as well as offices. 工程項目為建造及營辦一座五層高的大樓,提供車輛清洗和維修設施、 車輛停泊處及辦公室。

PART C (PERMIT CONDITIONS)

C部 (許可證條件)





<u>General Conditions</u> 一般條件

- 1.1 The Permit Holder and any person working on the Project shall comply with all conditions set out in this Permit. Any non-compliance by any person may constitute a contravention of the Environmental Impact Assessment Ordinance (EIAO) (Cap. 499) and may become the subject of appropriate action being taken under the EIAO.
- 1.2 The Permit Holder shall ensure full compliance with all legislation from time to time in force including, without limitation to, the Air Pollution Control Ordinance (Cap. 311), Waste Disposal Ordinance (Cap. 354), Water Pollution Control Ordinance (Cap. 358) and Noise Control Ordinance (Cap. 400). This Permit does not of itself constitute any ground of defence against any proceedings instituted under any legislation or imply any approval under any legislation.
- 1.3 The Permit Holder shall make copies of this Permit together with all documents referred to in this Permit and the documents referred to in <u>Part A</u> of the Permit readily available at all times for inspection by the Director or his authorised officers at all sites/offices covered by this Permit. Any reference to the Permit shall include all documents referred to in the Permit and also the relevant documents in the Register.
- 1.4 The Permit Holder shall give a copy of this Permit to the person(s) in charge of the site(s) and ensure that such person(s) fully understands all conditions and all requirements incorporated in the Permit. The site(s) refers to site(s) of construction of the Project and shall mean the same hereafter.
- 1.5 The Permit Holder shall display conspicuously a copy of this Permit on the Project site(s) at all vehicular site entrances/exits or at a convenient location for public's information at all times. The Permit Holder shall ensure that the most updated information about the Permit, including any amended Permit, is displayed at such locations. If the Permit Holder surrenders a part or the whole of the Permit, the notice he sends to the Director shall also be displayed at the same locations as the original Permit. The suspended, varied or cancelled Permit shall be removed from display at the Project site(s).
- 1.6 The Permit Holder shall construct and operate the Project in accordance with the project description in <u>Part B</u> of this Permit.
- 1.7 The Permit Holder shall ensure that the Project is designed, constructed and operated in accordance with the information and recommendations described in the approved EIA Report (Register No.: AEIAR-177/2013), the application document for environmental permit (Application No.: AEP-454/2013), other relevant documents in the Register, the information and mitigation measures described in this Permit, mitigation measures to be recommended in submissions that shall be deposited with or approved by the Director as a result of permit conditions contained in this Permit, and mitigation measures to be recommended under on-going surveillance and monitoring activities during all stages of the Project. Where recommendations referred to in the documents of the Register are not expressly referred to in this Permit, such recommendations are nevertheless to be implemented unless expressly excluded or impliedly amended in this Permit.
- 1.8 All deposited submissions, as required under this Permit, shall be rectified and resubmitted in accordance with the comments, if any, made by the Director within one month of the receipt of the Director's comments or otherwise as specified by the Director.
- 1.9 All submissions approved by the Director, all submissions deposited without comments by the Director, or all submissions rectified in accordance with comments by the Director under this Permit shall be construed as part of the permit conditions described in <u>Part C</u> of this Permit. Any variation of the submissions shall be approved by the Director in writing or as prescribed in the relevant permit conditions. Any non-compliance with the submissions may constitute a contravention of the Environmental Impact Assessment Ordinance (Cap. 499). All submissions or any variation of the submissions shall be certified by the Environmental Team (ET) Leader and verified by the Independent

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

un Gallena, NO. 18-24 Shan Mei Street, Fo Tan, N.T., Hong





Environmental Checker (IEC) referred to in Conditions 2.1 and 2.2 below, before submitting to the Director under this Permit.

- 1.10 The Permit Holder shall release all finalized submissions as required under this Permit, to the public by depositing copies in the Environmental Impact Assessment Ordinance Register Office, or in any other places, or any internet websites as specified by the Director, or by any other means as specified by the Director for public inspection. For this purpose, the Permit Holder shall provide sufficient copies of the submissions.
- 1.11 All submissions to the Director required under this Permit shall be delivered either in person or by registered mail to the Environmental Impact Assessment Ordinance Register Office (currently at 27/F, Southorn Centre, 130 Hennessy Road, Wanchai, Hong Kong). Electronic copies of all finalized submissions required under this Permit shall be prepared in Hyper Text Markup Language (HTML) (version 4.0 or later) and in Portable Document Format (PDF version 1.3 or later), unless otherwise agreed by the Director and shall be submitted at the same time as the hard copies.
- 1.12 The Permit Holder shall notify the Director in writing the commencement date of construction of the Project no later than one month prior to the commencement of construction of the Project. The Permit Holder shall notify the Director in writing immediately if there is any change of the commencement date of the construction.
- 1.13 For the purpose of this Permit, "commencement of construction works" does not include works related to site clearance and preparation, or other works as agreed by the Director.
- 1.14 The Permit Holder shall notify the Director in writing the commencement date of operation of the Project no later than one month prior to the commencement of operation of the Project. The Permit Holder shall notify the Director in writing immediately if there is any change of the commencement date of the operation.

2. Specific Conditions

Submissions and/or Measures before Commencement of Construction of the Project

Employment of Environmental Monitoring and Audit (EM&A) Personnel

- 2.1 An Environmental Team (ET) shall be established by the Permit Holder no later than one month before commencement of construction of the Project. The ET shall not be in any way an associated body of the Contractor or the Independent Environmental Checker (IEC) for the Project. The ET shall be headed by an ET Leader. The ET Leader shall be a person who has at least 7 years of experience in environmental monitoring and auditing (EM&A) or environmental management. The ET and the ET Leader shall be responsible for the implementation of the EM&A programme in accordance with the EM&A requirements as contained in the EM&A Manual of the Project. The ET Leader shall keep a contemporaneous log-book of each and every instance or circumstance or change of circumstances, which may affect the compliance with the recommendations of the EIA Report and this Permit. The ET Leader shall notify the IEC within one working day of the occurrence of any such instance or circumstance or change of circumstances. The ET Leader's log-book shall be kept readily available for inspection by all persons assisting in supervision of the implementation of the recommendations of the EIA Report and this Permit or by the Director or his authorized officers. Failure to maintain records in the log-book, failure to discharge the duties of the ET Leader as defined in the EM&A Manual of the Project or failure to comply with this Condition would entitle the Director to require the Permit Holder by notice in writing to replace the ET Leader. Failure by the Permit Holder to make replacement, or further failure to keep contemporaneous records in the log-book despite the employment of a new ET Leader may render the Permit liable to suspension, cancellation or variation.
- 2.2 An IEC shall be employed by the Permit Holder no later than one month before commencement of construction of the Project. The IEC shall not be in any way an associated body of the Contractor or the ET for the Project. The IEC shall be a person who has at least 7 years of experience in EM&A or

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com





environmental management. The IEC shall be responsible for duties defined in the EM&A Manual and shall audit the overall EM&A performance, including the implementation of all environmental mitigation measures, submissions required in the EM&A Manual, and any other submissions required under this Permit. In addition, the IEC shall be responsible for verifying the environmental acceptability of permanent and temporary works, relevant design plans and submissions under this Permit. The IEC shall verify the log-book(s) mentioned in Condition 2.1 of this Permit. The IEC shall notify the Director by fax, within one working day of receipt of notification from the ET Leader of each and every occurrence, change of circumstances or non-compliance with the EIA Report (Register No.: AEIAR-177/2013) and this Permit, which might affect the monitoring or control of adverse environmental impacts from the Project. In the case where the IEC fails to so notify the Director of the same, fails to discharge the duties of the IEC as defined in the EM&A Manual or fails to comply with this Condition, the Director may require the Permit Holder by notice in writing to replace the IEC. Failure to replace the IEC as directed or further failure to so notify the Director despite employment of a new IEC may render the Permit liable to suspension, cancellation or variation. Notification by the Permit Holder is the same as notification by the IEC for the purpose of this Condition.

Management Organization of Main Construction Company

2.3 The Permit Holder shall, no later than two weeks before the commencement of construction of the Project, inform the Director in writing the management organization of the main construction companies and/or any form of joint venture associated with the construction of the Project. The submitted information shall include at least an organization chart, names of responsible persons and their contact details.

Submission of Landscape and Visual Mitigation Plan of the Project

- 2.4 The Permit Holder shall, at least one month before the commencement of construction of the corresponding component(s) of the Project, submit four hard copies and one electronic copy of a Landscape and Visual Mitigation Plan(s) to the Director for approval. The Plan(s) shall include at least the following information:-
 - (a) one (1) existing tree to be retained in-situ at the location marked in Figure 2;
 - (b) a tree compensation proposal showing the locations, size, number and species of trees to be planted, including the compensation of at least 27 trees of heavy standard size (100mm DBH), in accordance with the recommended tree species in Table 1 and Table 2; and
 - (c) an updated landscape design for ground floor planting, vertical greening, roof gardens and hard landscape features.

The Landscape and Visual Mitigation Plan(s) shall be certified by the ET leader and verified by the IEC as conforming to the information and recommendations of landscape and visual mitigation measures contained in the EIA Report (Register No.: AEIAR-177/2013).

Submissions and/or Measures before and During Operation of the Project

Measures and Submission for Mitigating Landscape and Visual Impact before Operation of the Project

- 2.5 The landscape and visual mitigation measures shall be fully and properly implemented in accordance with the recommendations of the Landscape and Visual Mitigation Plan(s) approved under condition 2.4 above.
- 2.6 The Permit Holder shall, at least one month before the commencement of the operation of the Project, deposit with the Director four hard copies and one electronic copy of the As-Built Drawing(s) of the Project, which shall be certified by the ET Leader and verified by the IEC as conforming to the recommendations of the Landscape and Visual Mitigation Plan(s) approved under condition 2.4 above. The landscape and visual mitigation measures shall be properly maintained during operation of the

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Project.

Measures for Mitigating Odour Impact during Operation of the Project

- 2.7 All refuse collection vehicles shall be emptied of refuse prior to entering the Project.
- 2.8 To mitigate operational odour impact arising from the vehicle washing bays and the maintenance workshops of the Project:-
 - (a) the washing bays and maintenance workshops shall be enclosed in 3 sides and served with mechanical ventilations to maintain with proper negative air pressure at all times during the washing bays and maintenance workshops operation; and
 - (b) a deodorisation system, with an odour removal efficiency of at least 85%, shall be installed, operated and properly maintained at the ventilation system prior to discharging any vented air outside the Project.

Measures for Mitigating Noise Impact during Operation of the Project

- 2.9 To mitigate operational noise impact from the repair activities from the vehicles, the following measures shall be implemented:
 - (a) all vehicle repair activities shall be limited to 0700 to 1900 hours only; and
 - (b) all vehicle repair activities shall be carried out within the covered area of the transport workshop section on ground floor of the Project as shown in <u>Figure 2</u>.
- 2.10 To minimise off-site traffic noise impact arising from the operation of the Project, all vehicles coming in or out of the Project shall use the in-bound and out-bound traffic routing as shown in Figure 3.

3. Environmental Monitoring and Audit Requirements

- 3.1 The EM&A programme shall be implemented in accordance with the procedures and requirements as set out in the EM&A Manual. Any change to the EM&A requirements or programme shall be justified by the ET Leader and verified by the IEC as conforming to the relevant requirements set out in the EM&A Manual and shall seek the prior approval from the Director before implementation.
- 3.2 Samples, measurements and necessary remedial actions shall be taken in accordance with the requirements of the EM&A Manual by:
 - (a) conducting baseline environmental monitoring;
 - (b) conducting impact monitoring;
 - (c) carrying out remedial actions described in Event/Action Plans of the EM&A Manual in accordance with the time frames set out in Event/Action Plans, or as agreed by the Director, in case where specified criteria in the EM&A Manual are exceeded; and
 - (d) logging and keeping records of details of all parameters within 3 working days of the collection of data or completion of remedial action(s), for the purpose of preparing and submitting the monthly EM&A Reports and to make available for inspection on site.
- 3.3 Four hard copies and one electronic copy of the Baseline Monitoring Report shall be submitted to the Director at least 2 weeks before the commencement of construction of the Project. The submissions shall be certified by the ET Leader and verified by the IEC as complied with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of the submission shall be

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址 : http://www.telemaxeem.com





provided upon request by the Director.

- 3.4 Four hard copies and one electronic copy of monthly EM&A Report shall be submitted to the Director within 10 working days after the end of each reporting month throughout the entire construction period. The monthly EM&A Reports shall include a summary of all non-compliance. The submissions shall be certified by the ET Leader and verified by the IEC as complying with the requirements as set out in the EM&A Manual before submission to the Director. Additional copies of submission shall be provided upon request by the Director.
- 3.5 All EM&A data submitted under this Permit shall be true, valid and correct.

4. <u>Electronic Reporting of EM&A Information</u>

- 4.1 To facilitate public inspection of EM&A Reports via the EIAO Internet Website and at the EIAO Register Office, electronic copies of these Reports shall be prepared in Hyper Text Markup Language (HTML) (version 4.0 or later) and in Portable Document Format (PDF version 1.3 or later), unless otherwise agreed by the Director and shall be submitted at the same time as the hardcopies as described in Condition 3.3 and 3.4 of this Permit. For the HTML version, a content page capable of providing hyperlink to each section and sub-section of these Reports shall be included in the beginning of the document. Hyperlinks to all figures, drawings and tables in these Reports shall be provided in the main text from where the respective references are made. All graphics in these Reports shall be in interlaced GIF format unless otherwise agreed by the Director. The content of the electronic copies of these Reports must be the same as the hardcopies.
- 4.2 The Permit Holder shall, within six weeks after the commencement of construction of the Project, set up a dedicated web site and notify the Director in writing the Internet address where the environmental monitoring and project data is to be placed. All environmental monitoring data described in Condition 4.1 above shall be made available to the public via a dedicated web site to be set up by the Permit Holder in the shortest practicable time and in no event later than two weeks after the relevant environmental monitoring data are collected or become available, unless otherwise agreed with the Director. The Permit Holder shall maintain the dedicated website for public access of the environmental monitoring data and reports throughout the construction period of the Project, or otherwise as agreed by the Director.
- 4.3 The Internet website as described in Condition 4.2 above shall enable user-friendly public access to the monitoring and project data including the Project Profile, the approved EIA Report, the Environmental Permit(s) and all finalised submissions required under this Permit. The Internet website shall have features capable of:
 - (a) providing access to all environmental monitoring data collected since the commencement of works;
 - (b) providing access to all finalized submissions as required under this Permit;
 - (c) searching by date;
 - (d) searching by types of monitoring data; and
 - (e) hyperlinks to relevant monitoring data after searching;

or otherwise as agreed by the Director.

Table 1: Recommended Tree Species for Tree Compensation on Ground Floor*

Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

Tree Species suitable for Ground Floor Planting	g
Ailanthus fordii (Ailanthus)	Melaleuca quinquenervia (Paper-bark tree)

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com

160 team 150 team BIREAU VENTAS Certification

Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Bauhinia purpurea (Hong Kong orchid tree) Cassia surattensis (Sunshine Tree) Grevillea robusta (Silky Oak) Plumeria rubra (Red Frangipani) Terminalia mantaly (Madagascar Almond)

Table 2: Recommended Tree Species for Tree Compensation on Roof Garden*

Tree/Large Shrub Species suitable for Green Roof Planting					
Cassia surattensis (Sunshine Tree)	Osmanthus fragrans (Sweet Osmanthus)				
Lagerstroemia indica (Crape-myrtle)	Plumeria rubra (Red Frangipani)				

*Based on Tree Assessment Schedule in EIA Report Appendix 8-5

Notes:

註:

 This Permit consists of three parts, namely, <u>Part A</u> (Main Permit), <u>Part B</u> (Description of Designated Project) and <u>Part C</u> (Permit Conditions). Any person relying on this permit should obtain independent legal advice on the legal implications under the EIAO, and the following notes are for general information only.

本許可證共有3部,即<u>A部</u>(許可證主要部分);<u>B部</u>(指定工程項目的說明)及<u>C部</u>(許可證條件)。 任何援引本許可證的人士須就環評條例的法律含意徵詢獨立法律意見,下述註解只供一般參考 用。

- 2. If there is a breach of any conditions of this Permit, the Director or his authorized officer may, with the consent of the Secretary for the Environment, order the cessation of associated work until the remedial action is taken in respect of the resultant environmental damage, and in that case the Permit Holder shall not carry out any associated works without the permission of the Director or his authorized officer. 如違反本許可證的任何條件,署長或獲授權人員徵得環境局局長的同意後可勒令停止相關工程,直至許可證持有人為所造成的環境損害採取補救行動為止。在此情況下,許可證持有人未經署長或獲授權人員同意,不得進行任何相關工程。
- 3. The Permit Holder may apply under Section 13 of the EIAO to the Director for a variation of the conditions of this Permit. The Permit Holder shall replace the original permit displayed on the Project site by the amended permit. 許可證持有人可根據環評條例第13條的規定向署長申請更改本許可證的條件。許可證持有人須把 經修改的許可證替換在工程項目工地內展示的原有許可證。
- 4. A person who assumes the responsibility for the whole or a part of the designated project(s) may, before he assumes responsibility of the designated project(s), apply under Section 12 of the EIAO to the Director for a further environmental permit. 承擔工程項目整項或部分工程的責任的人,在承擔責任之前,可根據環評條例第12條的規定向署 長申請新的環境許可證。
- 5. Under Section 14 of the EIAO, the Director may with the consent of the Secretary for the Environment, suspend, vary or cancel this Permit. The suspended, varied or cancelled Permit shall be removed from display at the Project site. 根據環評條例第14條的規定,署長可在環境局局長的同意下暫時吊銷、更改或取消本許可證。遭暫時吊銷、更改或取消的許可證必須從工程項目工地除下,不再展示。
- 6. If this Permit is cancelled or surrendered during construction or operation of the Project, another environmental permit must be obtained under the EIAO before the Project could be continued. It is an offence under Section 26(1) of the EIAO to construct or operate a designated project listed in Part 1 of

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址 : http://www.telemaxeem.com





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

Schedule 2 of the EIAO without a valid environmental permit.

如果本許可證在工程項目建造或營辦期間取消或交回,則在繼續進行工程項目之前,必須先根據 環評條例規定取得另一份環境許可證。根據環評條例第26(1)條的規定,任何人在沒有有效環境許 可證的情況下建造或營辦環評條例附表2第1部所列明的指定工程項目,即屬犯罪。

- Any person who constructs or operates the Project contrary to the conditions in the Permit, and is convicted of an offence under the EIAO, is liable: 如任何人在違反本許可證的條件下建造或營辦工程項目,根據環評條例,即屬犯罪-
 - on a first conviction on indictment to a fine of \$2 million and to imprisonment for 6 months;
 一經循公訴程序首次定罪,可處罰款200萬元及監禁6個月;
 - (ii) on a second or subsequent conviction on indictment to a fine of \$5 million and to imprisonment for 2 years;

一經循公訴程序第二次或其後每次定罪,可處罰款500萬元及監禁2年;

- (iii) on a first summary conviction to a fine at level 6 and to imprisonment for 6 months;
 一經循簡易程序首次定罪,可處第6級罰款及監禁6個月;
- (iv) on a second or subsequent summary conviction to a fine of \$1 million and to imprisonment for 1 year; and

一經循簡易程序第二次或其後每次定罪,可處罰款100萬元及監禁1年;及

- in any case where the offence is of a continuing nature, the court or magistrate may impose a fine of \$10,000 for each day on which he is satisfied the offence continued. 在任何情況下如該罪行屬連續性質,法院或裁判官可就其信納該罪行連續的每一天另處罰 款10,000元。
- The Permit Holder may appeal against any condition of this Permit under Section 17 of the EIAO within 30 days of receipt of this Permit.
 許可證持有人可在接獲本許可證後30天內,根據環評條例第17條就本許可證的任何條件提出上 訴。
- The Notes are for general reference only and that the Permit Holder should refer to the EIAO for details and seek independent legal advice.
 上述註解只供一般參考用,欲知有關詳情,許可證持有人須參閱環評條例及徵詢獨立法律意見。

<u>Environmental Permit No. EP-454/2013</u> 環境許可證編號EP-454/2013

Figure 1 Figure 2 Figure 3

[Back to First Page] / [Back to Main Index]


-

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com






Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

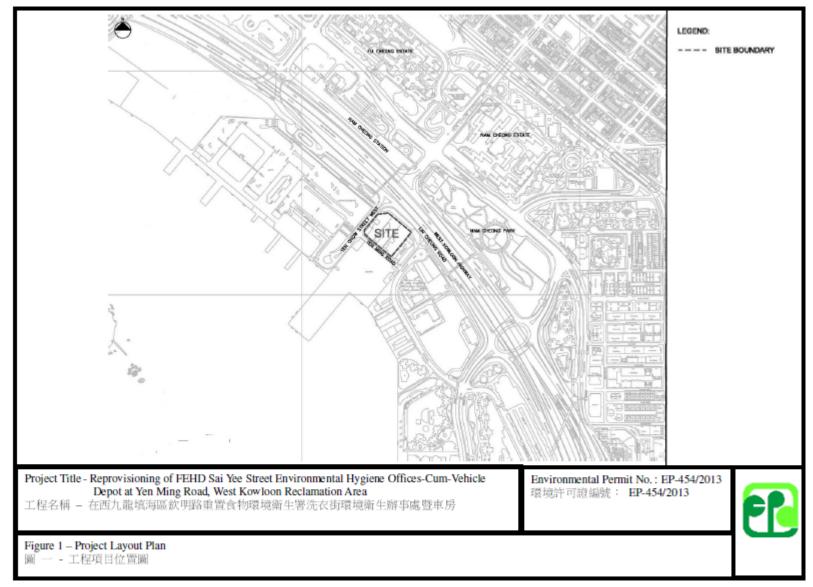






Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

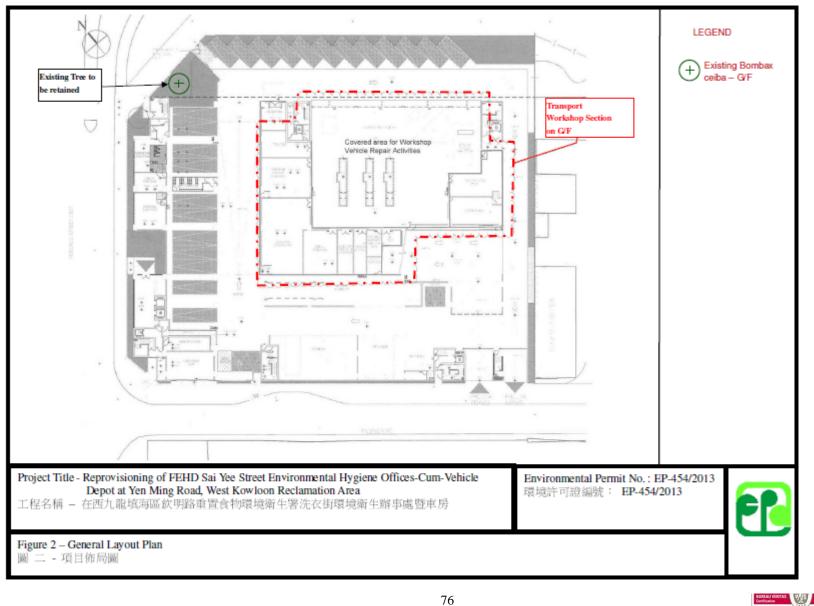


VKAS



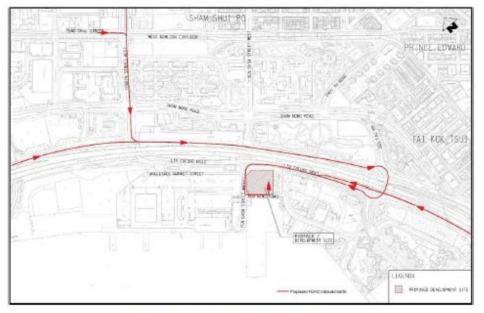

IN-BOUND TRAFFIC ROUTING

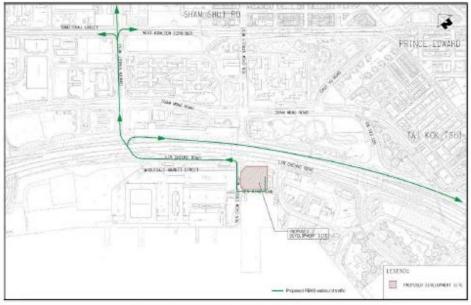

OUT-BOUND TRAFFIC ROUTING



香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

(b) Discharge License

WE/D/EPI 本署檔號 Our Ref: **Environmental Protection Department Environmental Compliance Division** EP482/269A/0017/I/164099 環保法規管理科 來函檔號 Regional Office (East) 區域辦事處(東) Your Ref. 5th Floor, Nan Fung Commercial Centre, 香港九龍九龍灣臨樂街 Tel. No.: 19 Lam Lok Street, Kowloon Bay, 十九號南豐商業中心五樓 圖文傳真 2117 7539 Kowloon, Hong Kong Fax No.: ECEIV 2756 8588 CC KKFu/ Telemix 電子郵件 E-Mail: 01 A 2/16 Homepage: http://www.epd.gov.hk/ RY: BY REGISTERED POST

China Road and Bridge Corporation Flat 07-11, 23A/F., K. Wah Centre, 191 Java Road, North Point, Hong Kong (Attn.: Chung Wai Hoi)

Dear Sir / Madam,

Water Pollution Control Ordinance (WPCO) Junk Bay / Port Shelter / Mirs Bay / Eastern Buffer / Victoria Harbour (Phase I / II) Water Control Zone <u>Application for a licence to discharge from</u> <u>Construction Site of Reprovisioning of Food and Environmental Hygiene Department</u> <u>Sai Yee Street Environmental Hygiene Offices-Cum-Vehicle Depot at Yen Ming Road,</u> <u>West Kowloon Reclamation Area</u>

In response to your above application dated <u>11 December 2015</u>, I enclose herewith a licence granted under the WPCO.

The granting of the licence <u>does not</u> imply that your discharge has complied with the licence's requirements. You should therefore read the terms and conditions of the licence carefully, particularly regarding the place, quality and rate of discharge as well as the sampling, treatment, disposal and site management requirements and ensure that they are fulfilled.

If there is any uncertainty about the terms and conditions of the licence, please contact $\underline{Ms \ Y \ L \ TSANG}$ at Tel. 2117 7546. If that is not resolvable, you may lodge an appeal in the prescribed manner and form with the Water Pollution Control Appeal Board within 21 days after receipt of the licence.

Thank you for your effort in protecting the environment.

Yours faithfully,

(CHAN Kin Ki) Environmental Protection Officer Regional Office (East) Environmental Compliance Division for Director of Environmental Protection

The Original WPCO Licence





掛號函件

先生/女士:

水污染管制條例 將軍澳/牛尾海/大鵬灣/東部緩衝區/維多利亞港(第一/二期) 水質管制區 <u>申領牌照於西九龍填海區欽明路重置食物環境衛生署洗衣街環境衛生辦事處暨車房</u> <u>之建築地盤排放污水</u>

有關你於 2015年12月11日 就上址申領污水排放牌照,本署現在附上按上述條例簽發的牌照,請你查收。

發出這牌照並非代表你的排放已符合牌照上的要求,你必須細閱牌照的條文和 條款,確保排放點、污水成份和流量、與及抽取樣本、處理設施、棄置及設施管理方 面能符合牌照要求。

若你就牌照的條文及條款有任何疑問,請致電 <u>2117 7546</u> 與 <u>曾玉玲</u>小 姐聯絡。如未能解決,你亦可在領到牌照後二十一日內,以指定的方式和表格,向水 污染管制上訴委員會提出上訴。

多謝你致力保護環境。

環境保護署署長 環保法規管理科 區域辦事處(東) (環境保護主任 陳健基 代行)

年月日

随函附件:水污染管制牌照正本




Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com





194	15200		
C.			
1	7	60	
		1	



ENVIRONMENTAL PROTECTION DEPARTMENT 環境保護署

WATER POLLUTION CONTROL ORDINANCE (CAP. 358) 水污染管制條例(第358章)

LICENCE PURSUANT TO SECTION 15/20/23A* 按第15/20/23A*條簽發的牌照

The Director of Environmental Protection ("the Authority") grants this licence under the Water Pollution Control Ordinance ("the Ordinance") on the terms and conditions stated below.

環境保護署署長(「監督」)按下列的條款及條件,根據水污染管制條例(「本條例」)批給此牌照。

22 January 2016

Date 日期

(CHAN Kin Ki) For *the Authority* 監督 (陳健基代行)

PARTA 甲部 : GENERAL TERMS 一般條款

Name of Licensee ("the Licensee")	China Road and Bridge Corporation
持 牌 人 名 稱 (「持 牌 人」)	中國路橋工程有限責任公司
Discharge Premises ("the premises") 排 放 處 所(「處 所」)	Construction Site of Reprovisioning of Food and Environmental Hygiene Department Sai Yee Street Environmental Hygiene Offices-Cum-Vehicle Depot at Yen Ming Road, West Kowloon Reclamation Area (See Annex) 西九龍填海區欽明路重置食物環境衛生署洗衣街環境衛生辦事處暨車房之 建築地盤(參考附件)
Water Control Zone	Victoria Harbour (Phase II)
水 質 管 制 區	維多利亞港(第二期)
Discharge Category	Discharge of Industrial/ Commercial/Institutional * Trade Effluent
排 放 種 類	工業/ 商業/機構 *污水排放
Nature of Discharge and Wastewater Treatment Facilities 排放性質及廢水處理設施	Effluent arising from construction site 由建築工程所產生的廢水 Sedimentation Tank 沉澱池
Discharge Point(s)	Discharge into communal storm water drain
排 放 點	排放入公用雨水渠
Sampling Point(s) 取 樣 點	Sampling point at discharge outlet of the treatment facilities 取樣點位於處理設施之出水口
'Delete as appropriate 將不適用者謝去	

Reference No. 参考编统 EP482/269A/0017/I/164099

- 1 -

EPD156





SPECIFIC CONDITIONS 特別條件 PARTB 乙部 :

B1. Limitations on Discharge 排放限制

The quantity and composition of any discharge from the premises shall not exceed the limits stated in the table below^(Note a). All figures are upper limits unless otherwise indicated. All units are expressed as concentration in milligramme per litre unless otherwise stated.

任何源自處所之排放的量和成份不得超過下表所列的限度。他用意。除另予表明外,所有數字均為上限。除另予說明 外,所有單位均以毫克/升的濃度表示。

外,所有单位与风电池的	
Determinand 測量物	Limit 限度
Flow Rate (m³/day)	20
流量 (立方米 / 日) Suspended Solids	30
懸浮固體	80
Chemical Oxygen Demand 化學需氧量	6-9#
pH (pH units) 酸鹼值(pH 單位)	

Range 上下限

B2. Self-monitoring and Reporting 自行監測及報告

- The Licensee shall perform self-monitoring as and when required by the Authority. \forall
- 持牌人須在監督要求時進行自行監測。
- The Licensee shall sample the discharge at the Sampling Point(s) and, at his own expense carry out analyses in accordance with the sample type and measurement frequency specified for each determinand named below:-持牌人須在取樣點為排放抽取樣本,並依照下列指定的測量物、取樣形式及頻率,自資予以分析。

Determinand 測量物 Unit 單 位	Sample Type 取樣形式	Frequency 頻 率
--------------------------	------------------	---------------

Results of these monitoring shall be summarized in a report on a monthly/bi-monthly/quarterly* basis and shall be submitted to the Authority.

所有監測結果須以摘要形式,每一個月/兩個月/三個月*作出紀錄,並呈交審閱。

*Delete as appropriate 將不適用者膨去

EPD156

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel: (852) 3563 7003 Fax: (852) 3563 7018 網址 : http://www.telemaxeem.com Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

- 2 -



PART C 丙 部 : STANDARD CONDITIONS 標 準 條 件

C1. The Discharge 排放

- C1.1 The discharge shall not contain polychlorinated biphenyls (PCB), polyaromatic hydrocarbon (PAH), fumigant, pesticide or toxicant, chlorinated hydrocarbons, flammable or toxic solvents, calcium carbide; any substance likely to damage the sewer or to interfere with any of the treatment processes, or to be harmful to the health and safety of any personnel engaged in the operation or maintenance of a sewerage system; waste liable to form scum or deposits in any part of the drainage or sewerage system, or the waters of Hong Kong; waste liable to form discolouration in any parts of the waters of Hong Kong; sludge, floatable substances or solids larger than 10 mm; and sludge or solid refuse of any kind. 排放不得含有多氢聯苯、聚芳烴、薰蒸劑、穀蟲劑或毒劑、氯化烴、可燃的或有毒的溶劑、碳化鈣; 會損毀污水渠結構或干擾任何處理程序的物質,或有損操作及維修排污系統人員健康及安全的任何物質;足以在排水或排污系統,或香港水域任何範圍內形成浮渣或沉積物的廢物;足以在香港水域任何範圍內形成變色的廢物;污泥、漂浮物質或體積超越10毫米的固體;及任何種類的污泥或固體垃圾。
- C1.2 No discharge shall bypass the wastewater treatment facilities, the Sampling Point(s) or the Discharge Point(s) unless it is unavoidable to prevent loss of life, personal injury or severe property damage or no feasible alternative exists.

除非避免人命傷亡或嚴重財物損失或無其他可行代替辦法,排放不得繞流不經其廢水處理設施,取樣點或 排放點。

C1.3 Dilution of the discharge to achieve compliance with the limits contained in this licence is prohibited. 不得將排放稀釋,以求達到本牌照內所訂的限度。

C2. Flow Measurement 量度流量

The Licensee shall determine the flow rate of the discharge by installing, operating and maintaining a continuous flow measuring device with an accuracy certified by its manufacturer to be within plus or minus 3 percent of the actual flow, and calibrating the flow measuring device regularly according to manufacturer's recommendations. If no such device is installed, the Licensee shall determine the flow rate through using calculation methods agreed by the Authority, by making reference to the amount of water used in the premises being served by mains supply and other sources, less process consumption and any other losses.

持牌人必須設置、操作及保養一個連續性流量計作為測定排放的流量率之方法,其準確程度須經製造商證實為不 超逾或低於真正流量的3%,並應根據製造商建議的方法,定期校準流量計。如沒有設置該設備,持牌人須依照 監督同意的計算方法,根據處所由自來水及其他水源供應的總用水量減去工序耗水量及其他耗水量來測定流量 率。

C3. Treatment 處理

C3.1 The Licensee shall provide necessary wastewater treatment facilities, and shall engage personnel with adequate qualification and experience to properly operate and maintain all wastewater treatment facilities at all times. Standby equipment shall be provided to guard against failure of major treatment equipment.

持牌人須提供必需的廢水處理設施,並須僱用有足夠資格及經驗的人士,時常妥善操作及保養所有廢水處 理設施。主要處理設施須配有後備裝置,以應付故障發生。

C3.2 In the event of loss of efficiency of operation, or failure of all or part of the wastewater treatment facility, the Licensee shall take all reasonable steps to the extent necessary to maintain compliance with this licence. Such steps shall remain until operation of the wastewater treatment facility is restored or an alternative method of treatment is provided.

倘若部份或整個廢水處理設施操作失靈或發生故障,持牌人須採取所有必要的合理措施,以求達到符合本 牌照的規定。此等措施須維持至廢水處理設施恢復如常操作或有其他代替的處理方法可供採用為止。

C3.3 If the wastewater treatment facilities are not properly operated and maintained to the satisfaction of the Authority, the Licensee shall take immediate and effective remedial actions as required by the Authority.

倘若廢水處理設施的操作及保養未能令監督滿意,持牌人須按監督之規定,採取即時及有效的補救行動。

C4. Disposal 棄置

Sludges, screenings, solids, oil and grease, filter backwash, or other pollutants removed in the course of treatment shall be disposed of in a proper manner^(Note b & c). 處理過程中所產生的污泥、隔濾物、固體、油脂、過濾器回洗或其他污染物,必須妥善地棄置^(ME b & c).

- 3 -

EPD156





C5. Monitoring 監測

- C5.1 The Licensee shall provide and maintain suitable facility such as an inspection chamber, manhole or sampling valve at each Sampling Point to enable duly authorized officer(s) of the Authority to take samples of the discharge at any time from the premises. 持牌人須在每一個取樣點提供及保養適當的設施,例如檢查槽,沙井或取樣閥,以確保獲監督授權的人員
- C5.2 For self-monitoring, "grab samples" shall be taken during the period when the determinand to be analyzed for is likely to be present in its maximum concentration. "Composite samples" shall include samples taken over daily duration of the discharge. 在自行監測中,「隨意取集樣本」須在測量物的濃度很可能是最高的那段時間內抽取。「綜合樣本」須包 含在每日排放期間不同時候所抽取的樣本。
- C5.3 For self-monitoring, all samples shall be analyzed in accordance with the most updated analytical methods used by the Government Chemist (Note dy). 在自行監測中,所有樣本均須按照政府化驗師所採用的最新分析方法予以分析 (Met d)。

C6. Records and Reporting 紀錄及報告

隨時可在處所內抽取排放樣本。

C6.1 The Licensee shall keep the following records in the premises for inspection by duly authorized officer(s) of the Authority:

持牌人須在處所內保存下列紀錄,以備獲監督授權的人員隨時查閱:

- records of flow rate, nature and composition of the discharge; 排放流量率、性質及成份的紀錄;
- (ii) updated records of all monitoring information, including all laboratory analytical results relating to samples taken, all original chart recordings for continuous flow and pH monitoring; and 所有最新監測資料的紀錄,包括所有關於已取樣本的檢驗分析結果、所有連續性流量及酸鹼值監測 記錄圖表的正本;及
- (iii) records of all desludging and degreasing operation, and records of corresponding disposal operation.

所有清除污泥和清理隔油池廢物工序的紀錄,及其棄置工序的紀錄。

Copies of all such records shall be submitted to the Authority upon request. 在監督要求時,須向監督呈交所有該等紀錄的副本。

C6.2 The Licensee shall notify and explain to the Authority within 24 hours upon the occurrence of an accidental discharge or any emergency bypass or an overflow of untreated effluent or an operation upset which places the discharge in a temporary state of non-compliance with this licence. The Licensee shall within 7 days following the incident, submit to the Authority a detailed report in writing on the cause and duration of the non-compliance. Reporting in accordance with this Condition does not relieve the Licensee of any obligations imposed by this licence.

倘若有未經處理的污水意外排放、緊急繞流或溢滿的事件或操作失靈,引至排放出現短暫不符合牌照規定 的情況,持牌人須在事發後24小時內立即知會監督並予以解釋。持牌人須在事故發生後7天內,以書面 報告,詳述事件的起因、違反牌照條件的時間及為減少、消除或防止類似事件再次發生所採取或將會採取 的措施,送交監督審閱。然而,按照本條件的規定提交報告並不表示持牌人可獲免除承擔本牌照內所載的 任何責任。

C7. Operation Manual 操作手冊

The Licensee shall prepare an operation manual which shall include, as a minimum, operating procedures, inspection programme and repair and maintenance programme for the wastewater treatment facilities. The operation manual shall be kept at the aforesaid wastewater treatment facilities and a copy of the manual shall be submitted to the Authority upon request.

持牌人須擬備廢水處理設施的操作手冊。手冊內容須最低限度包括操作程序、檢查、維修及保養工作計劃表。該 手冊須保存在上述廢水處理設施內。持牌人須在監督要求時,呈交手冊副本乙份。

C8. Notification of Change 更改通知

The Licensee shall notify the Authority in writing within 14 days of any changes or proposed changes in the processes of manufacture or the nature of the raw materials used or of any other circumstances which may alter the nature and composition of the discharge or may result in the permanent cessation of the discharge. 倘若持脾人更改或擬更改其生產程序、或所用原料的性質、或有其他足以改變其排放的性質及成份或可導致永久性終止排放的事情,必須在14日內以書面通知監督。

- 4 -

EPD156

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com

100 MM1 ISO 1001 BUREAUVERITAS Certification

Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



Not	es 附註
(a)	For the purposes of determining compliance with the limits stated in Specific Condition B1, samples shall be taken by the duly authorized officer(s) of the Authority at the Sampling Point(s) or any other points from which the samples so taken are regarded by the Authority as being representative of the quality of the discharge. When any single sample analyzed for a determinand is proved not complying with corresponding limit set out in the table, the discharge is deemed to have failed to comply with Specific Condition B1. Samples and the samples and the samples are regarded by the samples are regarded by the failed to comply with Specific Condition B1. Samples are regarded by the samples ar
	的樣本的任何其他位置抽取樣本。只要在任何一個經分析的樣本中,證實任何一個測量物不有古來中的5%的是的是不及。 排放即被視為不符合特別條件第 B1項。
(b)	An example of proper disposal method for sludge is sending dewatered sludge to landfill for disposal. 妥善棄置污泥方法中的一個例子是將脫水後的污泥運往堆填區棄置。
(c)	Proper disposal of grease trap waste includes but is not limited to employing any reputable firm or collector who will use the right equipment and dispose of the collected grease trap waste at West Kowloon Transfer Station. The updated list of grease trap waste collectors who are using the disposal service at West Kowloon Transfer Station is maintained in the EPD website and Green Restaurant website.
	妥善的隔油池廢物棄置方法包括卻不限於聘用任何信譽良好的公司/收集商使用適富的設備在四九龍廢物轉運站棄且所 收集的隔油池廢物。環保署網站及環保食肆網均載有目前使用西九龍廢物轉運站棄置隔油池廢物的收集商最新名單。
(d)	The Licensee may make reference to Annex 1 of the <technical effluent="" memorandum="" on="" standards=""> for analytical methods used</technical>
	by the Government Chemist. 持牌人可參照「流出物標準技術備忘錄」附件1有關政府化驗師所採用的分析方法。
(e)	The Licensee shall keep this licence in the premises and make it available at all times for inspection by duly authorized officer(s) of
	the Authority. 持牌人須在處所內保存此牌照,以備獲監督授權的人員隨時查閱。
Ø	(i) The Licensee shall allow duly authorized officer(s) of the Authority to enter the premises for the purposes of inspection, sampling, records examination or any other duties authorized by Section 37 and Section 38 of the Ordinance. 持牌人须准許獲監督授權的人員進入處所內進行檢查、抽取樣本、審查紀錄或執行其他根據本條例第 37 及第 38 條 所授權的職務。
	 (ii) Where the premises has security measures in force which would require proper identification and clearance before entry, the Licensee shall make necessary arrangements such that upon presentation of evidence of identity and of authorization, duly authorized officer(s) will be permitted to enter, without delay, for the purposes of performing duties. 倘若由於處所的保安理由而需先行鑑定來人的身份,持牌人必須作出必要的安排,以便獲授權人員在出示身份證明及授權文件後,即可內進執行其職務而不致受延誤。
(g)	(i) For a licence granted under Section 15 of the Ordinance, the Licensee may, not less than 2 months before expiry of the licence, apply under Section 19 of the Ordinance for a new licence. The Authority may grant the licence or otherwise. 持有根據本條例第 15 條所批給牌照的人士,可於牌照屆滿前不少於 2 個月內,根據本條例第 19 條的規定,申請一面新牌照。監督可批給或拒絕批給牌照。
	 (ii) For a licence granted under Section 20 or 23A of the Ordinance, the Licensee may, not more than 4 months and not less than 2 months before expiry of the licence, apply under Section 23 or 23A respectively of the Ordinance for renewal of licence.
	The Authority may renew the licence or otherwise. 持有根據本條例第 20 條或第 23 A 條所批給牌照的人士,可於牌照屆滿前不多於 4 個月及不少於 2 個月內,根據本 條例的第 23 或 23 A 條的規定,申請牌照續期。監督可將牌照續期或拒絕將牌照續期。
(h)	licence or cancel this licence. Under Section 25, 26 and 27 of the Ordinance, a Licensee whose ficence has been so varied of
	cancelled may be entitled to compensation. 根據本條例第 24 條的規定,監督可以書面通知,向本牌照施加新訂或經修訂的條款及條件,或取消本牌照。根據本條例 第 25、26 及 27 條的規定,被更改或取消牌照的持牌人可能會獲得補償。
(i)	Under Section 28 of the Ordinance, the Licensee may apply to the Authority for a variation of this licence. 根據本條例第 28 條的規定,持牌人可向監督申請更改本牌照。
(j)	Under Section 49 of the Ordinance, this licence shall not be construed as a dispensation from the requirements of any other Ordinance except where that other Ordinance so provides. 根據本條例第 49 條的規定,本牌照並不得解釋為豁免符合任何其他條例的規定,除非該其他條例如此訂定。
(k)	The licensee should ensure good practice is carried out in dealing with discharges from the construction site. The licensee should make reference to the EPD's Practice Note for Professional Persons, No. PN 1/94, "Construction Site Drainage". 持牌人須確保妥善處理地盤之去水排放。持牌人可參考環保署印發之 Practice Note for Professional Persons, 編號 PN 1/94, "Construction Site Drainage"


香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong



- 5 -

Telemax Environmental and Energy Management Limited Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



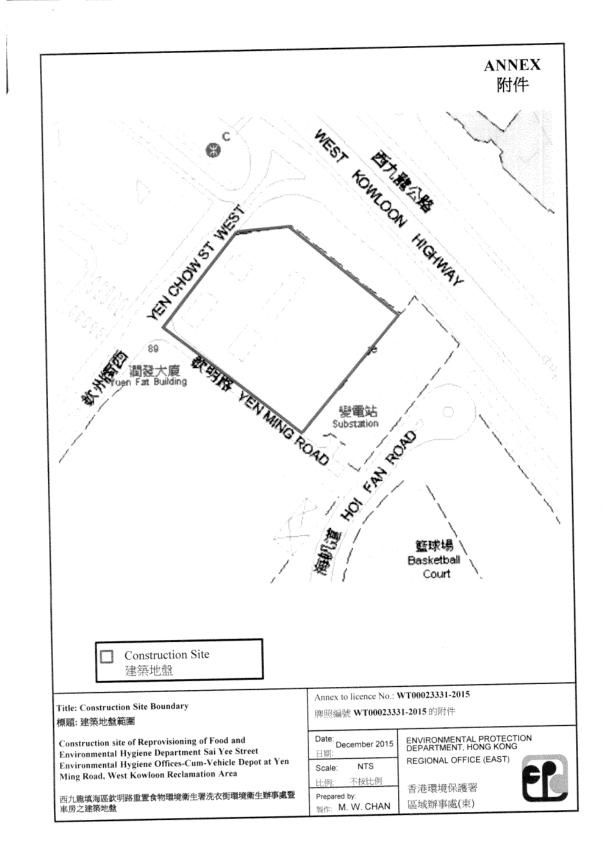





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com (c) Chemical Waste Producer Registeration

本著指統 Our Ref: 来函格號 396912 Your Ref: 電 話 Tel. No.: 2117 7539 圖文傳真 Fax No.: 2756 8588 電子郵件 E-Mail: 纲 近 Homepage: http://www.epd.gov.h <u>By Registered Po</u>	DI	CC. W	環境保護署 環保法規管理科 區域辦事處(東) 香港九龍九龍海臨筆街 十九號南聖商業中心五樓 ノの(EPD 10 JAN 2016 CC KFFu/ Tele www.
Dear Sir/Madam,			

Waste Disposal Ordinance (Cap. 354) Waste Disposal (Chemical Waste) (General) Regulation Registration as a Chemical Waste Producer <u>Completion of Registration</u>

I am pleased to inform you that your registration with this department as a chemical waste producer has been completed.

The assigned Waste Producer Number (WPN) and the particulars of your establishment are printed in the enclosed form (EPD 130). If you consider there are any discrepancies about the particulars, please notify me immediately, quoting the assigned WPN.

The "EPD 130" is an important document, please archive appropriately. This registration is not transferable and will be valid only in respect of the applicant and the premises registered. In future when there is change in the registration particulars, you should inform this department as soon as possible so that our record can be amended accordingly. Under section 7 of the above regulation, failure to notify this department of relevant changes is an offence and liable to a maximum fine of HK\$10,000.

For enquiries, please contact us at Tel 2117 7546.

Yours faithfully,

(CHAN Kin Ki) Environmental Protection Officer for Director of Environmental Protection

Encl.





Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

	Environmental Protection Department 環境保護署					
1	Waste Disposal Ordinance (Chapter 354)					
1	香港法例第354章廢物處置條例					
	Waste Disposal (Chemical Waste)(General) Regulation 廢物處置(化學廢物)(一般)規例					
1		Registration of Waste Producer				
⊢		廢物產生者登記證				
To: 致	Chemical Waste Producer	Vaste 全 名 (英 文) CHINA ROAD AND BRIDGE CORPORATION				
	化學廢物產	(Chinese) 中國路橋工程有限責任公司 I.D. Card No. (if any) (中 文)				
	生者	Business Reg. Cert. No. (if any) 商業登記證號碼: (如有者) 16058447-000-08-15-A				
		Address for Correspondence				
		通訊地址: FLAT 07-11, 23A/F., K.WAH CENTRE, 191 JAVA ROAD, NORTH POINT, HONG				
		KONG				
		Tel. No. Fax No. 電話: 2283 1688 圖文傳真: 2283 1689				
	With referen	nce to your application dated 11 / 12 / 2015 for registration as a Waste				
	Producer un	nder the Waste Disposal (Chemical Waste) (General) Regulation, the Waste Producer Number,				
		2 1 3 - 2 6 9 - C 1 2 3 2 - 1 8 is assigned to you in respect of the location or premises				
	listed below					
)	前於 <u>2015</u>	2年_12_月_11_日 根據廢物處置(化學廢物)(一般)規例而來信,申請登記為廢物產生者,茲特配				
2	予廢物產生者	編號第 52113-269-01232-18 號·予下開地點或處所:				
	Location or	Name of Establishment CHINA ROAD AND BRIDGE CORPORATION 機構名稱: 中國路橋工程有限責任公司				
	Premises where the	Business Reg. Cert. No. (if any) 16058447-000-08-15-A				
	waste is	岡 来 立 記 證 號 嚩:(如月者)				
	produced	Nature of Business 業務性質: CONSTRUCTION SITE				
	產生廢物	Major chemical waste types				
	的地點或	主要化學廢物種類:SURPLUS PAINT, SPENT LUBRICATION OIL				
	處所					
		Address REPROVISIONING OF FOOD AND ENVIRONMENTAL HYGIENE DEPARTMENT SAI 地:				
		YE STREET ENVIRONMENTAL HYGIENE OFFICES-CUM-VEHICLE DEPOT AT YEN				
	MING ROAD, WEST KOWLOON RECLAMATION AREA					
	Church Ch					
	(CHAN Kin Ki)					
		tor Director of Environmental Protection 環境保護署署長(陳健基 代行)				
		Date 15 1 2016 日期				
WAI	RNING : A	ny registered waste producer who fails to inform the Director of Environmental Protection of any				
警	ci	hange in his registration particulars commits an offence and is liable on conviction to a fine of \$10,000. E何已登記的廢物產生者,若其登記資料有任何改變而不知會環境保護署署長,即屬違法,被定罪者最高罰款				
		±幣10,000元。				

EPD 130

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong




(Nov 2012)



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

(d) Billing Account for Disposal of Construction Waste



Waste Disposal (Charges for Disposal of Construction Waste) Regulation Approval of Application for Billing Account (Construction work contract with value of \$1 million or above) Application No.: <u>RT01354</u>

I am pleased to inform you that your application for billing account for disposal of construction waste under the following construction work contract has been approved under Section 6 and 9 of the Waste Disposal (Charges for Disposal of Construction Waste) Regulation:

Contract No.: SS D505

Contract Name: REPROVISIONING OF FEHD SAI YEE STREET ENVIRONMENTAL HYGIENE OFFICES-CUM-VEHICLE DEPOT AT YEN MING ROAD, WEST KOWLOON RECLAMATION AREA (PROGRAMME NO. 182GK)

Construction Waste Generated Site: YEN MING ROAD, WEST KOWLOON RECLAMATION AREA

The account number is <u>7024032</u>. Please quote this account number for enquiries in relation to the billing account.

You are bound by the "Basic Conditions" and "Conditions of Use" accompanied with this account for disposal of construction waste at the prescribed facilities. You shall ensure that (a) the billing account established solely for the contract as stated above is used for paying any prescribed charge payable in respect of construction waste generated from construction work undertaken under the above contract; and (b) that billing account is <u>not</u> used for paying any prescribed charge payable in respect of any other construction waste <u>not</u> generated from construction work undertaken under the contract as stated above.

Regarding your application for issuance of chits, a demand note for the deposit required will be sent to you accordingly. Request for additional chits can be made using "Form 4". Please note that one chit is required for each load of construction waste to be disposed of at prescribed facility.

Should you have any queries, please contact us at 2872 1769.

Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

Yours faithfully,

(C F Wong) Principal Environmental Protection Office for Director of Environmental Protection

14



AN 25 MA

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com





(e) Construction Noise Permit



SSD505/SL/PTA/0441 Our Ref: : Date: : 22 December 2017

P&T Architects and Engineers Ltd. 33/F, 633 Kings Road, North Point, Hong Kong

Attn: Ms Clara Pang

Dear Madam,

Construction Noise Permit for CRBC (GW-RE0978-17)

(Contract No. SSD505)

Reprovisioning of FEHD Sai Yee Street Environmental Hygiene Offices-cum-vehicle Depot at Yen Ming Road

1. Enclosed please find the captioned Construction Noise Permit for CRBC (renewed on 18/12/2017) for your reference.

2. Should you have any queries, please feel free to contact me at 97793814.

Yours faithfully, For and on behalf of China Road and Bridge Corporation KEF

K K Fu (Site Agent)

c.c

()	AECOM (CDM/SRM)	w/o Encl., E-mail
(X)	PTME Group e-mail	With Encl, E-mail + Hard copy
(X)	PTS Group e-mail	With Encl, E-mail
(X)	ArchSD (TA) - Mr Charles Tang	w/o Encl., E-mail
(X)	ArchSD (ER-BSI) - Mr M W Ho	w/o Encl., E-mail
(X)	ArchSD (COW) - Mr W Y Choi	w/o Encl., E-mail
(X)	ArchSD (PM) - Mr Dick Wan	w/o Encl., E-mail + Hard copy
(X)	ArchSD (SPM) - Mr Tse Lok Man	w/o Encl., E-mail

(X)	AECOM (BEAM) - Group e-mail	With Encl., E-mail
(X)	AEC - Mr T K Ho	With Encl., E-mail
(X)	L&S Group e-mail	w/o Encl., E-mail
(X)	PTS - R.E. Mr. Alvin Lam	With Encl., E-mail
(X)	COW - Mr Marco Leung	With Encl., E-mail
(X)	BSI – Mr K C Pang	With Enel., E-mail
(X)	CRBC - Head Office	With Encl., E-mail
(X)	CRBC - Site Office	With Encl., E-mail



Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

音 准 北 角 道 車 道 1 9 1 戦 嘉 単 御 際 中 心 1 8 字 線 1 8 0 5 堂 1 0 空 Units 1005-10, 18年, K. Wah Centre, 191 Java Road, Moth Pohit, Hong Kong, 電話 7 et; 1652-2283 1 688 (伊夏 Fax: 863-2283 1 689 電子部第 E-mail: crbchk@crbc.com.hk 韻 Website: www.crbc.com

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



環境保護署

18 December 2017

環保法規管理科

區域辦事處(東)

九龍長沙灣道 303 號

長沙灣政府合署8樓

Registered Post

To:

China Road and Bridge Corporation Flat 07-11, 23A/F., K.Wah Centre, 191 Java Road, North Point, Hong Kong.

Dear Sirs,

Notice of Issue of Construction Noise Permit pursuant to section 8(6) of the Noise Control Ordinance (Cap. 400)

Environmental Protection Department

Environmental Compliance Division

8/F., Cheung Sha Wan Government Offices

Regional Office (East)

303 Cheung Sha Wan Road

Kowloon

I write to inform you that, under section 8(6) of the Noise Control Ordinance, the Authority has decided to issue a construction noise permit in respect of your application, which was received by the Authority on 04 December 2017, for the use of powered mechanical equipment for carrying out construction work at <u>Construction site at junction of Yen Chow</u> <u>Street West and Yen Ming Road, West Kowloon Reclamation Area, Mong Kok, Kowloon</u>.

The construction noise permit No. GW-RE0978-17 is enclosed.

You are advised to read the conditions of the permit carefully and to ensure compliance with these conditions. Any breaching of the conditions may lead to cancellation of the permit, subsequent prosecution action and the Authority's refusal to issue further permit for the above construction site.

Yours faithfully,

(YIP Ka Fan) for Authority



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



(4) in EP631/K03/RE423977-17

2150 8017 2402 8275

掛號函件

致: 香港 北角 渣華道 191 號 嘉華國際中心 23A 樓 07-11 室 中國路橋工程有限責任公司

執事先生:

根據《噪音管制條例》(第400章)第8(6)條 發出的通知書 — 簽發「建築噪音許可證」

本監督在二零一七年十二月四日接獲你擬於<u>九龍旺角西九龍填海區欽州街西與欽</u> 明路交界的建築地盤,使用機動設備進行建築工程而提出的「建築噪音許可證」申請, 現根據《噪音管制條例》第8(6)條的規定通知你,上述的申請已被批准。

隨函附上「第 GW-RE0978-17 號建築噪音許可證」。

請細閱許可證各項條件,確保遵守。如有違反,本監督可撤銷許可證、提出檢控及 拒絕再就上述地盤簽發任何「建築噪音許可證」。

監 督

(葉嘉勲

代行)

二零一七年十二月十八日



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



[reg.5(a)]

FORM 3 NOISE CONTROL ORDINANCE (Chapter 400) SECTION 8(9)

CONSTRUCTION NOISE PERMIT FOR THE USE OF POWERED MECHANICAL EQUIPMENT FOR THE PURPOSE OF CARRYING OUT CONSTRUCTION WORK OTHER THAN PERCUSSIVE PILING AND/OR THE CARRYING OUT OF PRESCRIBED CONSTRUCTION WORK

CONSTRUCTION NOISE PERMIT NO. GW-RE0978-17

To: China Road and Bridge Corporation

This construction noise permit is issued in accordance with section 8 of the Noise Control Ordinance. Permission is granted for the use of powered mechanical equipment for the purpose of carrying out construction work other than percussive piling and/or the carrying out of prescribed construction work, subject to the conditions set out below. The carrying out of construction work otherwise than in accordance with the conditions may result in the permit being cancelled and in a prosecution for an offence.

CONDITIONS

 Construction site where the powered mechanical equipment and/or prescribed construction work may be employed : Full address : Construction site at junction of Yen Chow Street West and Yen Ming Road, West Kowloon Reclamation Area, Mong

Kok, Kowloon.. Lot No.: ---

The site boundary, that is, the boundary of the area within which the powered mechanical equipment may be used and the prescribed construction work may be carried out is delineated on the attached plan which forms part of this construction noise permit.

2. * PART/WHOLE of the site falls * WITHIN/OUTSIDE a designated area.

3. Powered Mechanical Equipment

a. Items of powered mechanical equipment which may be used inside the site boundary :

Identification code of item of powered mechanical equipment (if applicable)		on of item of anical equipment	No. of uni
	Refer to attached sheet		
alidity of the construction noise permit	for the use of the powered mechani	ical equipment:	
alidity of the construction noise permit Date and time of commencement :	for the use of the powered mechani 03 January 2018	ical equipment: at	1900 hours
	03 January 2018	at	
Date and time of commencement :	03 January 2018 general holiday (including Sunda	at y), 0000-0700 hours	s and 1900-2400 hours on any da
Date and time of commencement : Days and hours : 0000-2400 hours on being a general holiday . [but note con mechanical equipment is allowed]	03 January 2018 general holiday (including Sunda	at y), 0000-0700 hours	s and 1900-2400 hours on any da
Date and time of commencement : Days and hours : 0000-2400 hours on being a general holiday . [but note con	03 January 2018 general holiday (including Sunday dition 3.d.1. below for the operation 30 June 2018 hority, of each item of powered m	at y), 0000-0700 hours ag hours within whi at nechanical equipme	s and 1900-2400 hours on any da ch the use of the above listed por 2300 hours and described in this construction

Refer to attached sheet EPD76A(s) - 1 -

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

150 MRT 150 MRT 2007 Confidentian 2007 Confident



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com

- 4. Prescribed Construction Work
 - a. Type of prescribed construction work which may be carried out inside the site boundary :

	Identification code of type of prescribed construction work	P	Description of type prescribed construction	
		Nil		
		1.00	r orde	
b.	Validity of the construction noise permi	it for the carrying out of the prese	ribed construction wor	k:
	Date and time of commencement :	03 January 2018	at	1900 hours
	Days and hours : 0000-2400 hours o	n general holiday (including Sun	day), 0000-0700 hours	s and 1900-2400 hours on any day n
	being a general holiday.			en de la compañía de la
	This part of the permit expires on :	30 June 2018	at	2300 hours
	of prescribed construction work described available for inspection by the Au Other conditions imposed on the carryin	thority.		
		NAMES OF TAXABLE PARTY.		
	s construction noise permit or a copy the			
	ormation			
inf	ormation.		Sind	M
inf	ormation.	ember 20 <u>.17</u>		La Farry
Date	ormation.	ember 20 <u>.17</u>	(YIP K	La Farry
Date	ormation. ed this 18 th day of Dec.	ember 20 <u>.17</u>	(YIP K	La Farry
Date	ormation. ed this 18 th day of Dec.	ember 20 <u>.17</u>	(YIP K	La Farry



Tel.: (852) 3563 7003 Fax: (852) 3563 7018 www.telemaxeem.com



[第5(a)條]

- - -

表格3 嗓音管制條例 (第400章) 第8(9)條

建築噪音許可證 為進行建築工程(撞擊式打樁除外) 而使用機動設備及/或進行訂明建築工程

建築噪音許可證編號: GW-RE0978-17

致: 中國路橋工程有限責任公司

本建築噪音許可證是按照《噪音管制條例》第8條的規定而發出的。現准予使用機動設備以進行撞 擊式打樁工程以外的建築工程及/或進行訂明建築工程,但須受以下條件規限。若不按照該等條件 進行建築工程,許可證可遭撤銷,而且會受到檢控。

條件

1. 可使用機動設備及/或進行訂明建築工程的建築地盤:

詳細地址:九龍旺角西九龍填海區欽州街西與欽明路交界的建築地盤。

地段編號:

地盤範圍(即可使用機動設備及進行訂明建築工程的地方範圍)已描劃於夾附的圖則上,而該 圖則是本建築噪音許可證的一部分。

- 2. 該地盤部分/全部*位於指定範圍之內/外*。
- 3. 機動設備
 - a. 在地盤範圍內可使用的各項機動設備:

各項機動設備的識辨代碼 (如適用的話)	各項機動設備的說明	數目
	參見附頁。	
ويرغب إستراحه والا		

b. 可使用機動設備的建築噪音許可證有效期:

生效日期及時間:	二零一八年一月三日	下午七時
日期及時間: 公眾假日(包括星	期日)的凌晨零時至晚上十二時	持,公眾假日以外的任何一
日凌晨零時至上午七時及下午廿	二時至晚上十二時 【 但 須 注 意	t條件3.d.1.有關可以使
用上列機動設備的時間】。		
此部分許可證屆滿日期及時間:		晚上十一時 時間
	F1 774	11-4
建築地盤須備有本建築嗓音許可 等照片須經監督認可。	證所延每件機動設備的照片各	一幀,供監督隨時查看;該
規限使用機動設備的其他條件:		
參見附頁。		
5)	-1-	
	日期及時間: 公眾假日(包括星日凌晨零時至上午七時及下午 用上列機動設備的時間】。 此部分許可證屆滿日期及時間: 建築地盤須備有本建築嗓音許可 等照片須經監督認可。 規限使用機動設備的其他條件: 參見附頁。	日期及時間: 公眾假日(包括星期日)的凌晨零時至晚上十二時 日凌晨零時至上午七時及下午七時至晚上十二時 <u>【</u> 俱須注意 <u>用上列機動設備的時間</u> 】。 此部分許可證屆滿日期及時間: 二零一八年六月三十日 日期 建築地盤須備有本建築噪音許可證所述每件機動設備的照片各 等照片須經監督認可。 規限使用機動設備的其他條件: 參見附頁。





- 4. 訂明建築工程
 - a. 在地盤範圍內可進行的訂明建築工程:

訂明建築工程的識辨代碼 訂明建築工程的類別的說明 無 b. 可進行訂明建築工程的建築噪音許可證有效期: 生效日期及時間: 二零一八年一月三日 下午七時 日期及時間: 公眾假日(包括星期日)的凌晨零時至晚上十二時,公眾假日以外的任何一 日凌晨零時至上午七時及下午七時至晚上十二時。 此部分許可證屆滿日期及時間: 二零一八年六月三十日 晚上十一時 日期 時間 c. 本許可證可夾附經監督認可的地盤圖則,以顯示本許可證准予進行訂明建築工程的地點。 該地盤圖則須存放於建築地盤供監督隨時查看。 d. 規限進行訂明建築工程的其他條件: 5. 本建築噪音許可證或其副本必須展示於建築地盤的所有車輛人口/出口處,給予公眾人士參 閱。 日期:2017 年 12 月 18 日 簽署: 監督 (葉嘉勲 代行) * 刪去不適用者 -2-





Sheet attached to Construction Noise Permit No. <u>GW-RE0978-17</u>

3.a. Items of powered mechanical equipment which may be used inside the site boundary :

Identification code of item oj powered mechanical equipment (if applicable)		Description of item of powered mechanical equipment	No. of units
Group A CNP 044		Concrete lorry mixer	One
	CNP 049	Crane, tower (electric)	One
		Generator, with Quality Powered Mechanical Equipment Label showing a Sound Power Level of ≤ 99 dB(A)	One
	CNP 283	Water pump, submersible (electric)	Twenty
<u>Group B</u>		Poker, vibratory, hand-held (electric)	Two
	CNP 283	Water pump, submersible (electric)	Twenty
<u>Group C</u>	CNP 283	Water pump, submersible (electric)	Twenty

Signed: (YIP Ka Fan) for Authority





建築噪音許可證 編號 <u>GW-RE0978-17</u>的附頁

3.a. 在地盤範圍內可使用的各項機動設備:

各項機動設備的識辨代碼 (如適用的話)		各項機動設備的說明		
<u>A 組</u>	CNP 044	混凝土攪拌車	壹	
	CNP 049	起重機,塔型(電動)	壹	
		發電機,備有優質機動設備標籤顯示聲功率級≦99 分貝(A)		
	CNP 283	潛水泵 (電動)	貳拾	
<u>B 組</u>		混凝土震動機,手提(電動)	貳	
107	CNP 283	潛水泵 (電動)	貳拾	
<u>C 組</u>	CNP 283	潛水泵 (電動)	貳拾	

簽署:

<u>監督</u> (葉嘉勲 代行)





Page 2 of 2

Sheet attached to Construction Noise Permit No. <u>GW-RE0978-17</u>

3.d. Other conditions imposed on the use of the powered mechanical equipment:

1. The powered mechanical equipment listed in condition 3.a. shall only be operated during the hours shown below:

Current A to Current D	General holiday (including Sunday)	0700 – 2300 hours		
Group A to Group B	Any day not being a general holiday	1900 – 2300 hours		
Group C	Any day	2300 – 0700 hours on next day		

2. Only one group of the powered mechanical equipment listed in condition 3.a. shall be allowed to operate at any time.

Signed : YIP Ka Fan) for Authority





共二頁,頁二

建築噪音許可證 編號 <u>GW-RE0978-17</u>的附頁

3.d. 規限使用機動設備的其他條件:

1. 祇可於以下時間內使用列在條件3.a.內的機動設備:

4 41 万 万 41	公眾假日(包括星期日)	上午七時至晚上十一時		
A組至B組	公眾假日以外的任何一日	下午七時至晚上十一時		
C 組	任何一日	晚上十一時至翌日上午七時		

2. 在任何時間內, 祇可使用列在條件3.a.內的其中一組機動設備。



簽署:

監督 (葉嘉勲 代行)



1



Photograph attached to Construction Noise Permit No. <u>GW-RE0978-17</u> 建築噪音許可證編號<u>GW-RE0978-17</u>的照片



CNP 044 Concrete lorry mixer 混凝土攪拌車



CNP 049 Crane, tower (electric) 起重機,塔型(電動)





Photograph attached to Construction Noise Permit No. <u>GW-RE0978-17</u> 建築噪音許可證編號<u>GW-RE0978-17</u>的照片

N.S.	から RIE 類別	發電機			
	Type 製造商 / 牌子	Generator			
	Manufacturer / Trade N 型號	lame AIRMA	N		
	Model 編號	SDG300S-3A1			
	Serial Number 聲功率級	ENHG00			
	Sound Power Level 識別號碼	99	分貝(A) dB(A)		
	QPME ID Code	EPD-0044	16		
	Issued by Enviro	Omental D+	環境保護署簽	授 /	
S.		mental Prote	ction Departme	nt	
and the second	and the second	2 the course			
				_	
1	永發電	機	祥	13	
	× **	*	祥		

showing the Sound Power Level of \leq 99 dB(A) 發電機,備有優質機動設備標籤顯示聲功率級 \leq 99 分貝(A)

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel.: (852) 3563 7003 Fax.: (852) 3563 7018 網址: http://www.telemaxeem.com Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong


SO NOT SO HORT SUBJECT VERTICS Certification Certification n I



Photograph attached to Construction Noise Permit No. <u>GW-RE0978-17</u> 建築噪音許可證編號GW-RE0978-17的照片



CNP 283 Water pump, submersible (electric) 潛水泵 (電動)

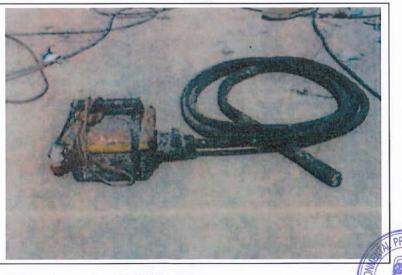

Poker, vibratory, hand-held (electric) 混凝土震動機,手提 (電動)













Appendix N NSR 1 School Calendar 2017-18

Sir Ellis Kadoorie Secondary School (West Kowloon) School Calendar 2017-2018

Month	Week	Sun	Mon	Tue	Wed	Thu	Fri	Sat		Holidays, Special Days & Examinations
2017							1	2	1	First Day of School Year
September	1	1	543	5	6	7	8	9	4	Festival of Eid
(20 school days)	2	X	11	12	13	14	13	16	15	Sports Day (Heats)
	3	X	18	4	20	21	22	23	19	Sports Day (Finals)
	4	X	25	26	27	28	29	30		
	5	\times	X	3	4	~	6	7	2	The Day following National Day
October	6	1	9	10	11	12	13	14	5	The Day following the Mid-Autumn Festival
(18 school days)	7	\mathbf{x}	16	17	18	19	2013	21	20, 21	Festival of Diwali, Festival of Bhai Tika
(8	X	63	24	25	60	27	X	23, 24-31	1st Staff Development Day, 1st Term Test
	9	1	30	200 C		and the second s	the	ai	28	Chung Yeung Festival
	-	10			1	2	2	4		
November	10	1	6	7	8	9		11	10	Parents' Night & AGM of PTA
(22 school day)	11	\sim	13	14	15*	16		18	15, 17	Friday Timetable, P6 Information Day & Fun Fair
(22 school day)	12				22	23*		25	23, 24	Friday Timetable, School Picnic
	12	~	20	21		100	/24	25	23, 24	Priday Timetable, School Pichic
	15		27	28	29	- 30				
								2		
December	14	\mathcal{X}	4	5	6	7	/8	9	6, 8	Speech Day Final Rehearsal, Speech Day
(15 school days)	15	10	11	12	13	14	15	16	11-15	ESTP Challenge Camp for S2 & S3
	16	X	18	19*	20	2	22	23	19, 21	Friday Timetable, Talent Show & Class Party
		X	2	20	27	28	29	30	22/12-1/1	Christmas and New Year Holidays (11 days)
		X								
2018	17			2	3	4	5	6	1	The First Day of January
January	18	1	(2)	Õ	60	0	Ô	13	8-22	Half-yearly Exam, Mock Exam for S6
(21 school days)	19	-	ñ	Tie I	ñ	TR I	l the	20	23	Post-Exam Activities
(at scanne mays)	20		65	12	24*	65	26	20	24, 25	Thursday Timetable, 2nd Staff Development Day
	20	-1	200	1 100 2	31	V.Y	20	21	24, 26-31	Discussion of Exam Papers
	21		2.9	- 30	31			_		
_						1	2	3	1	2nd Term Commences
February	22	\checkmark	5	6	7	8	<u>_</u> 9	10	9	Parents' Day
(12 school days)	23	$\boldsymbol{\lambda}$	12	13*	14	15	10	X	13	Friday Timetable
		10	19	20	21	22	23	24	14-25	Lunar New Year Holidays (11 days)
	24	X	26	27	28					
							2	3	1	S6 Graduation Day
March	25		5	6	7	8	9	10		
(21 school days)	26		12	13	14	15*		17	15, 16	Friday Timetable, Learning Celebrations and PTA Night
(at scattor mays)	27		19	20	21	[22]	23	24	22-29	2nd Term Test
	28		26	27	28	29		14	30/3-8/4	Easter Holidays (9 days)
	20		1201	-		14		2	5	Ching Ming Festival
A	29			3	4		6			Chillig Millig Pestivat
April			9	10	11	12	13	14		
(15 school days)	30	×,	16	17	18	19	20	21		
	31	X	23	- QA	3	26	27	28	24, 25	S3 TSA Oral Examination
	32	X	হাট							
					2	3	4	5	1	Labour Day
May	33	1	7	8	9	10	11	12		
(20 school days)	34	X	14	15		17	18	19	16	3rd Staff Development Day
	35	X	21	25	23	24	25	26	22	The Birthday of the Buddha
	36	X	28	29	30	31				-
							1	2		
June	37	1	4	5	6	\bigcirc	Ø	9	6-22	Yearly Examination & S3 TSA Examination
(20 school days)	38		Ū.	Ô	Ő	65	- The second sec	16	18	Tuen Ng Festival
(20 school days)	39			K	8	- M	6		25-28	Discussion of Examination Papers
	40		10					23		•
		14	2.5	26	27	28	29	-30	29/6-9/7	Post-Exam Activities
	41		1	Δ	4	15	6	7	2	The Day following HKSAR Establishment Day
July	42	1		20	11	12	13	14	10, 11	Last School Day & Variety Show, Release of HKDSE Results
(6 school days)		X	16	17	18	19	20	21	12, 13	S.1 Registration
		X	23	24	25	26	27	28	17	Pre-S.1 Attainment Test
		15	30	31					11/7-31/8	Summer Vacation (52 days)
					1	2	3	4		
Aug		1	6	7	8	9	10	11	20	All Staff should be available in Hong Kong
		10	13	14	15	16	10	18	22, 23	Induction of New Teachers, HOD & HOC Meetings
		12	20	21		10	1/	25	22, 25	
		0	720	41	122	723	_	25	24	1st Staff Meeting, CT & ACT Meeting Orientation Day for S1-S6 New Students
			21	128	29	30	31		28	Orientation Day for 51-50 ivew Students
	~				~	,				
	()	Examin	ation Perio	đ	53	Discretion	ary Holiday	18	No. of Scho	ol Days: 190



No. of School Holidays & Discretionary Holidays: 90 + 3

香港沙田火炭山尾街 18-24 號沙田商業中心 16 樓 9-10 室 Tel: (852) 3563 7003 Fax: (852) 3563 7018 網址: http://www.telemaxeem.com

Unit 9-10, 16/F, Shatin Galleria, No. 18-24 Shan Mei Street, Fo Tan, N.T., Hong Kong

School Holidays Public Holidays

Special Timetable



9
