

中國建築安樂聯營



China State – ATAL Joint Venture

Contract No. DC/2009/17

Harbour Area Treatment Scheme Stage 2A
Upgrading Works at Stonecutters Island Sewage
Treatment Works – Sludge Dewatering Facilities

Revision No. 0

WASTE MANAGEMENT PLAN

	Position	Name	Signature	Date
Prepared By:	Environmental Officer	H. S. Lui		3 rd December 10
Approved By:	Site Agent	Chris LEUNG		3 rd December 10

CONTENTS

1. INTRODUCTION	5
1.1 BACKGROUND	5
1.2 PURPOSES OF THE WMP	6
1.3 WASTE MANAGEMENT REQUIREMENTS AND GUIDELINES	7
1.4 LICENCES REQUIREMENTS	8
2. ORGANISATION AND STRUCTURE	9
2.1 ORGANIZATION AND RESPONSIBILITY	9
3. IDENTIFICATION AND CLASSIFICATION OF WASTE GENERATED FROM THE CONSTRUCTION ACTIVITIES	11
3.1 WASTE ARISING FROM THE CONSTRUCTION ACTIVITIES	11
3.1.1 Excavated Material	11
3.1.2 Marine Deposit	11
3.1.3 Construction & Demolition Materials	12
3.1.4 General Refuse	12
3.1.5 Chemical Waste	12
3.2 DESIGNATED WASTE DISPOSAL FACILITIES AND DISOPOSAL CRITERIA	12
4. PROPOSAL FOR WASTE MANAGEMENT	14
4.1 WASTE MANAGEMENT HIERARCHY	14
4.2 DESGIN AND PLANNING OF CONSTRUCTION WORKS	14
4.3 WASTE MINIMIZATION MEASURES AND GOOD SITE PRACTICE	15
4.4 HANDLING OF C&D MATERIALS	16
4.4.1 Waste Sorting	16
4.4.2 Chemical Waste	18
4.5 PROMOTION AND TRAINING ON WASTE MANAGEMENT	19
4.5.1 Environmental Training	19
4.5.2 Environmental Promotion	20
5. TRIP TICKET SYSTEM AND RECORDING	21
5.1 TRIP TICKET SYSTEM (TTS)	21
5.2 WASTE RECORDING SYSTEM	22

6. EVENT CONTINGENCY PLAN FOR NON-COMPLIANCE	23
6.1 HANDLING PROCEDURE FOR NON- COMPLIANCE AND COMPLAINT	23
6.2 ENVIRONMENTAL EMERGENCY PROCEDURES FOR CHEMICAL SPILLAGE	24
7. AUDITING PROPOSAL	25

Appendices

Appendix A	Project Organization Chart for Waste Management
Appendix B	Tentative C&D Materials Disposal Programme (Monthly Schedule)
Appendix C	General Layout Plans for On Site Waste Management
Appendix D	Waste Classification and Their Recommended Usage / Outlet
Appendix E	Monthly Summary of Waste Flow Table & Record of Timber Usage
Appendix F	Sample of CHIT, Disposal Delivery Form & Daily Summary Record

Tables

Table 3.1	Estimated Volume of C&D Material Generated during the Project Works (DC/2009/17)
Table 3.2	Designation of Public Fill Reception Facility and Landfill
Table 4.1	Waste Management Hierarchy

1.0 INTRODUCTION

In accordance with Section 9.152 of the EIA report (register no. AEIAR-121/2008), a Waste Management Plan (WMP) shall be prepared for submission to Environmental Protection Department (EPD).

1.1 Background

This report will outline the Contractor WMP proposed by the Contractor for DSD Contract (Contract No. DC/2009/17) Harbour Area Treatment Scheme Stage 2A (HATS 2A), Upgrading Works at Stonecutters Island Sewage Treatment Works – Sludge Dewatering Facilities. China State – ATAL Joint Venture (CSAJV) will ensure that all his employees will implement the accepted version of this WMP as an integral part of their daily activities on site.

This project consists of the construction of Sludge Dewatering Building, Northern and Southern Sludge Cake Silos, Northern and Southern Sludge Conveyor Bridges, two Sludge Storage Tanks, Deodourization Units No. 5 and 6, Workshop Building, Water Storage Tanks and demolition of the existing sludge cake silos and sludge dewatering building inside the Stonecutters Island Sewage Treatment Plant area. This project was commenced in August 2010 and the works would take place in a 69-month period.

There are five sections of Work with different scopes of this Contract include the following items:

■ **Section 1A of the Works**

At the commencement of work, temporary vehicle washing facilities will be constructed within the area of the existing sludge cake silo. After completion of the temporary facilities, the existing vehicle washing facilities can be demolished to facilitate the piling works at the Sludge Dewatering Building.

■ **Section 2 of the Works**

The design of the piling works will be submitted to the Engineer for approval as soon as possible after commencement of the works. At the same time, initial works such as pre-drilling for the pre-bored H-piles will also be proceeded.

The pile at Northern Sludge Cake Silo and Sludge Dewatering Building can be commenced once the founding level of the piles has been confirmed. The piles along the side of the proposed tunnel to be constructed under Contract DC/2009/05 will be installed first so that the piles will be completed before the tunnel construction. Some of these piles at Sludge Dewatering Building can only be proceeded after the demolition of the existing vehicle washing facilities.

■ **Section 3 of the Works**

This section is to complete construction of the Northern Sludge Cake Silo, the Northern Conveyor Bridge, the Sludge Dewatering Building, the Sludge Storage Tanks and the associated pipe works and commission the system. Piling work at the Northern Sludge Cake Silo and Sludge Dewatering Building will be continued after achievement of Section 2 of the Works. The structural works and E&M installation proceed after piling. The steelwork of the Northern Sludge Cake Silo and the Conveyor Bridge will be fabricated in Mainland. The prefabricated units will be delivered to site by marine

transport. Heavy duty crane will be employed to lift up the units and install the units in position.

Construction of the Sludge Storage Tanks 6&7 will be commenced upon possession of the site at the commencement of the works. The pipe works and ducting will be installed and connected to the Northern Sludge Cake Silo and Sludge Dewatering Building.

After testing and commissioning, the existing sludge dewatering building and sludge cake silo will be decommissioned.

■ **Section 4 of the Works**

After decommissioning, the plant and equipment inside the existing sludge dewatering building and sludge cake silo will be removed, and the structures demolished.

■ **Section 5 of the works**

Diversion of the existing drainage and ducting will be carried out for construction of the new Water Tanks as soon as completion of Section 3 of the Works. When the new Water Tanks are ready, the existing ones will be demolished so that the some of the piles at the new Workshop Building can be installed.

Construction of the Southern Sludge Cake Silo, the Southern Conveyor Bridge and the Workshop Building commences after existing structures have been demolished. Daido piles will be re-driven and tested before installation of the prebored H-piles at the Workshop Building.

All the remaining external works will be carried out concurrently with the structural works. After E&M installation, the completed system will be tested and put into operation.

1.2 Purposes of the Waste Management Plan

This WMP provides necessary technical information, guidance and instructions to designated personnel who are responsible for the management of Construction and Demolition Materials (C&DM).

The aims of this WMP are:

- To identify and classify the types of C&DM generated in the execution of the works;
- To identify the potential for reuse, recycling minimization and disposal of C&DM from the proposed construction activities; and
- To outline the implementation, monitoring and audit programmed to ensure that the wastes arising from the construction activities are handled, stored, collected, transferred and disposed of in an environmentally acceptable manner which complies with the contract requirements and the relevant *Ordinance* and *Regulations* in the Government of Hong Kong SAR.

"C&DM" refers to surplus materials arising from any land excavation or formation, civil/building construction, road works, building renovation or demolition activities. It includes various types of the reusable materials, building debris, rubble, earth, concrete, timber and mixed site clearance materials. When sorted properly materials suitable for land reclamation

and site formation (known as public fill) should be reused at public filling area whereas the remaining C&D wastes are to be disposed of at landfills.

This WMP will also describe the waste management arrangements for other wastes (such as chemical waste, general refuse) that will be generated during the construction activities.

1.3 Waste Management Requirements and Guidelines

During the contract period, CSAJV will comply with the following legislations, code of practices, guidelines, practical notes and technical circulars.

■ Statutory requirements

- *Waste Disposal Ordinance (Cap. 354) and its subsidiary regulations;*
- *Waste Disposal (Chemical Waste) (General) Regulation (Cap. 354);*
- *Public Health and Municipal Services Ordinance - Public Cleansing and Prevention of Nuisances Regulation (Cap. 132);*
- *Land (Miscellaneous Provisions) Ordinance;*
- *Dumping at Sea Ordinance (Cap. 466); and*
- *Dangerous Goods Ordinance (Cap.295)*

■ Codes of Practice, Circulars and Guidelines

CSAJV will meet all relevant requirements by consulting the following codes of practice, technical circulars and guidelines:

- a. *Environment, Transport and Works Bureau Technical Circular (Works) No. 15/2003 - Waste Management on Construction Sites;*
- b. *Environment, Transport and Works Bureau Technical Circular (Works) No. 19/2005 Environmental Management on Construction Sites*
- c. *Environment, Transport and Works Bureau Technical Circular No. 33/2002 - Management of Construction and Demolition Material Including Rock;*
- d. *Works Bureau Technical Circular No. 21/2002 - Trip-ticket System for Disposal of Construction and Demolition Material;*
- e. *Works Bureau Technical Circular No. 12/2002 - Specifications Facilitating the Use of Recycled Aggregates;*
- f. *Works Bureau Technical Circular No. 06/2002A - Enhanced Specification for Site Cleanliness and Tidiness;*
- g. *Works Bureau Technical Circular No. 06/2002 - Enhanced Specification for Site Cleanliness and Tidiness;*
- h. *Works Bureau Technical Circular No. 19/2001 - Metallic Site Hoardings and Signboards;*
- i. *Works Bureau Technical Circular No. 12/2000 - Fill Management;*
- j. *Works Bureau Technical Circular No. 04/1998A - Use of Public Fill in Reclamation and Earth Filling Projects;*
- k. *Works Bureau Technical Circular No. 04/1998 - Use of Public Fill in Reclamation and Earth Filling Projects;*
- l. *Works Bureau Technical Circular No. 16/1996 - Wet Soil in Public Dumps;*
- m. *Works Bureau Technical Circular No. 02/1993B - Public Filling Facilities;*

- n. *Works Bureau Technical Circular No. 02/1993 - Public Dumps;*
- o. *Works Bureau Technical Circular No. 32/1992 - The Use of Tropical Hardwood on Construction Sites;*
- p. *A Guide to the Registration of Chemical Waste Producers;*
- q. *A Guide to the Chemical Waste Control Scheme;*
- r. *Code of Practice on the Packaging, Labeling and Storage of Chemical Wastes;*
- s. *Code of Practice on the Handling, Transportation and Disposal of Asbestos Waste – (Cap 354, Section 35) and,*
- t. *Environmental Guidelines for Planning in Hong Kong (1990), Hong Kong Planning and Standards Guidelines, Hong Kong Government.*

CSAJV will observe all applicable statutory requirements, legislation and associated regulations, and/or code of practices with regard to the waste to be generated in the construction activities. CSAJV will also apply all necessary permits and licenses under these ordinances / regulations

1.4 License Requirements

Where appropriate, CSAJV will apply for all permits and licenses required under the following legislation for the handling and disposal of waste arising from the Project:

- a. *Chemical Waste Producer Registration under the Waste Disposal (Chemical Waste) (General) Regulation; and,*
- b. *License to Collect and Transport Chemical Waste under Waste Disposal Ordinance*
- c. *Public Dumping License under the Land (Miscellaneous Provisions) Ordinance.*

A licensed chemical waste collector will be appointed for the disposal of chemical waste. Upon classification of any types of chemical waste as dangerous goods under the Dangerous Goods Ordinance, the handling of these wastes will comply with all the requirements of the ordinance and its regulations.

2.0 ORGANISATION AND STRUCTURE

This Section provides an outline of the roles and responsibilities of the major site staff involved with the management of C&DM arising from the Project.

2.1 Organization and Responsibility

The Site Manager will have the overall responsibility to ensure that the requirements of the WMP are properly implemented. He will act as the Waste Manager for the Contract. The Site Agent acts as Deputy Waste Manager and Team Leader of the Environmental Team for overall control of waste management practices to ensure compliance with the contract requirements. The responsibilities of key site staff for the WMP are listed as follows: (see Appendix A of Project Organization Chart).

Site Manager, SM (Waste Manager)

The Project Manager will maintain overall control of all aspects of the construction activities and will oversee the implementation of the WMP. He is also responsible for ensuring that there are adequate resources available for the implementation of the WMP. He will also chair the ad hoc meeting(s) with the Supervising Officer's Representatives to discuss the WMP.

Site Agent (Deputy Waste Manager and Team Leader)

The Site Agent will be responsible for management and control of the construction activities in relation to waste management and mitigation measures. He will be responsible for assigning other team members to assist him for supervision and enforcement of the on-site waste management practices. The Site Agent will be responsible for:

- *Identification and classification of all possible wastes arising from the construction activities*
- *Analysis of effectiveness, efficiency and reliability of waste reduction programme*
- *Obtaining all necessary licenses and permits for the handling and disposal of wastes*
- *Planning for on-site segregation, sorting and storage of wastes*
- *Ensure that the on-site waste management practices are in compliance with all legislations and requirements of the Contract*
- *Carry out quarterly internal auditing for the implementation of WMP*
- *Provide resources to the implementation and control of the WMP*

Environmental Officer, EO

- *Identify legal requirements*
- *Ensure site comply with legal requirements*
- *Prepare, implement and update the WMP*
- *Update the Waste Flow Table and Use of Timber Record*
- *Verify waste management activities and related results to comply with planned arrangements*
- *Arrange and provide the environmental training including the site specific induction training and toolbox talks*
- *Organize environmental promotional activities*
- *Liaise on all matters relating to complaint, enquiry and non-compliance*
- *Carry out environmental system audits*

**Environmental Supervisor, ES;
Safety Officer and Assistant Safety Officer (Team Member)**

- Identify statutory requirements, contract requirements and corporation requirements
- Identify material that can be recycled, re-use and returned
- Arrange re-use, recycle and return work
- Monitor sub-contractors and workers to implement according to WMP
- Conduct waste management briefing to all site staff and workers
- Carry out quarterly internal auditing for the implementation of WMP

General Foreman (Team Member)

- Prepare location plans for storage of building materials to avoid or minimize construction materials damage on site
- Ensure WMP is implemented and maintained
- Instruct relevant parties to solve management problems
- Instruct and monitor sub-contractors and workers to implement according to WMP
- Carry out monthly review for the implementation of WMP

Foremen (Team Member)

- Assist General Foreman to prepare location plans for storage of building materials to avoid or minimise relevant materials damage on site
- Arrange sorting facilities for waste materials re-use and recycling
- Arrange waste materials storage areas and disposal of waste materials according to Trip-ticket System
- Ensure that daily site cleanliness and tidiness are implemented
- Instruct and monitor sub-contractors and workers to implement according to WMP
- Carry out weekly review for site cleanliness and tidiness

Subcontractor Representatives (Team Member)

- Ensure that construction waste are properly sorted out and disposed
- Ensure that construction waste are properly reused and recycled
- Coordinate with foremen to rectify and take follow-up actions for identified waste management issues
- Provide adequate resources for the implementation of WMP
- Direct and supervise workers to implement according to WMP

Workers

- Follow the instructions given by General Foreman, Foremen or Subcontractor Representatives to carry out waste management issue on site
- Reduce construction waste generation on site if possible
- Ensure that construction waste are properly sorted, re-used, recycled or returned on site
- Maintain good housekeeping of the workplaces after daily work activities

3.0 IDENTIFICATION AND CLASSIFICATION OF WASTE GENERATED FROM THE CONSTRUCTION ACTIVITIES

3.1 Waste Arising from the Construction Activities

Major activities that will generate waste from this Project include site clearance, excavation, demolition works, formwork construction for concreting, etc.; which can be divided into distinct categories based on their composition as follows:

- excavated materials from foundation work and underground services works;
- C&DM from demolition, structural, architectural and external works;
- chemical waste from maintenance of plant and equipment; and
- general refuse from construction workers.

A summary of the estimated quantities of C&D material to be generated from the construction and demolition work under the Project is shown in Table 1 below and the tentative C&D material disposal programme is attached in [Appendix B](#).

Table 3.1 Estimated Volume of C&D Material Generated during the Project Works (DC/2009/17)

Works Items	Inert C&D Material			Total A+B+C (m ³)
	Soft Materials A (m ³)	Grade III or better Rock (hard inert material) B (m ³)	Concrete C (m ³)	
Sludge Holding Tanks	3,100	-	-	3,100
Sludge Dewatering Building	5,350	-	-	5,350
Sludge Cake Silos	910	-	-	910
General Ground Works and Utilities	1,700	-	-	1,700
Existing Sludge Dewatering Building (Demolition)	-	-	2,092	2,092
Total Inert C&D Material Generation	11,060	-	2,092	13,152

3.1.1 Excavated Material

The excavated material generated from excavation will consist of soil and rock materials which will, as far as practicable, be reused on-site for the backfilling works. Excavated material will also be generated from foundation work, underground services works and even any temporary works for excavation. Any surplus excavated material will be disposed of site.

3.1.2 Marine Deposit

No marine deposit is identified / planned to be disposed of under this Contract. The estimated marine deposit from HATS 2A upgrading works at SCISTW would be excavated under other contract.

3.1.3 Construction & Demolition (C&D) Materials

C&D materials include inert public fill materials such as bricks, rubble, concrete and non-inert C&D waste such as wood, steel, vegetation and office and work force waste etc. The majority of C&D material will arise during site clearance, demolition and excavation works.

3.1.4 General Refuse

The workforce will likely generate general refuse comprising food scraps, waste paper, empty containers, etc.

3.1.5 Chemical Waste

The maintenance and servicing of construction plant and equipment generates chemical waste, for instance, cleaning fluids, solvents, lubrication oil and used batteries. The maintenance of vehicles also uses common chemicals, oil, lubricants and paints for this purpose.

A summary table regarding waste classification and recommended usage / outlet is shown in Appendix C. The handling / management of each waste type are detailed in Section 4.

3.2 Designated Waste Disposal Facilities and Disposal Criteria

The designation of public fill reception facility and landfill, the possible disposal routes and the relevant criteria as stipulated in the Waste Disposal (Designated Waste Disposal Facility) Regulation (Cap 354L) are summarized in Table 2.

Table 3.2 Designation of Public Fill Reception Facility and Landfill

C&D Material	Designated Waste Disposal Facility	Designated Location	Possible Disposal Routes to Designated Location	Criteria to be adopted
Inert C&D Material	Public Fill Reception Facilities	Tuen Mun Area 38 Fill Bank	Stonecutters Island, West Kowloon Expressway, Tsing Kwai Highway, Cheung Tsing Tunnel, Ting Kau Bridge, Tai Lam Tunnel, Route 3, Yuen Long Highway, Tuen Mun Road, Lung Mun Road	Entirely of inert construction waste (Schedule 5)
C&D Waste	Landfills	North East New Territories (NENT) Landfill	Stonecutters Island, Ching Cheung Road, Tai Po Road, Tolo Highway, Fanling Highway, Sha Tau Kok Road, Wo Keng Shan Road	For a load of construction waste delivered by a vehicle, the weight of the waste divided by the permitted gross vehicle weight of the vehicle must not be greater than 0.25 for goods vehicle with demountable skip and 0.2 for other types of vehicles (GN6395)

CSAJV will also comply with the following requirement when delivery of construction waste to public fills reception facilities and landfills:

- (1) Any over-sized inert C&D materials will be broken down to less than 250mm in size so as to facilitate its re-use by other reclamation or earth-filling project.
- (2) CSAJV will implement proper measures to ensure that the dump trucks delivering C&D materials are not overloaded.
- (3) C&D material to be disposed to the public fill shall be free from pond mud according to the conditions of the dumping license.
- (4) Mixed C&D material should be sorted at source to reduce the inert content to less than 30% by weight as far as practicable before they are delivered to landfills.
- (5) The C&D waste delivered for landfill disposal shall contain no free water and the liquid content shall not exceed 70% by weight.

4.0 PROPOSAL FOR WASTE MANAGEMENT

4.1 Waste Management Hierarchy

CSAJV will implement appropriate waste management practices according to the nature and category of wastes arising. Waste management options will be selected according to the widely accepted hierarchy shown by Table 3 below.

Table 4.1 Waste Management Hierarchy

↓	Avoidance and minimization	Avoid and minimize waste through changing or improving practices and designs.	↑
	Reuse of materials (with limited reprocessing)	Reuse construction waste with only limited reprocessing such as uncontaminated soil, wooden planks, metals and other materials in other construction works or process.	Highest priority
	Recovery and Recycling (may require reprocessing)	Undertaking on site or off site recycling.	Lowest priority
	Treatment	Offsite destruction and detoxification etc, of wastes into less harmful substances.	
	Disposal	Release of wastes to designated areas properly so as to render them harmless.	

The hierarchy will be used to evaluate waste management options for the minimization of waste generation. By the implementation of this hierarchy, the overall construction cost will be reduced by avoiding the over-ordering of construction materials and the handling and disposing of unnecessary waste.

4.2 Design and Planning of Construction Works

Prior to commencement of works, CSAJV will carefully consider the construction methodology, demolition procedures and programme to assess the waste generation during works and study the available opportunity to reduce waste arising. Good work planning will, not only result in a better estimation of materials required for the works, but also contribute to the performance of the works in the first instance so as to avoid abortive activity.

Prior to the commencement of works, the location and necessary facilities for construction material storage, on site sorting and temporary waste collection will be planned and implemented. The opportunity for the reuse and recycling of the waste material on site and off site will be carefully studied.

A general layout plans for the chemical waste storage area and the proposed storage/ sorting area for C&D material are attached in Appendix D.

4.3 Waste Minimization Measures and Good Site Practice

Good management and site practice can prevent the over generation of waste. Waste reduction is best achieved at the planning and design stage as well as by ensuring the implementation of good site practice. The good site management to be adopted will include:

- a. *Using the correct amount of raw materials at the correct time and the recording of materials flow to minimize over ordering. The construction materials will be stocked carefully to prevent damage or contamination. During the works, only exact quantity of materials will be collected and if necessary, any surplus will be returned to stock after consideration of its use;*
- b. *Maximizing the utilization of materials and the avoidance of unnecessary cutting such that off-cuts will be used when short lengths or a small quantity of materials are required;*
- c. *A preference for reusable non-timber formwork such as steel formwork or plastic facing;*
- d. *Sorting of all excavated / demolition materials to recover the inert portion (e.g. soil and broken rock) for reuse on site whenever possible or disposal to designed outlets (e.g. public filling areas). Recover all metal, cardboard and paper on site and properly stored in dry and clean conditions temporarily for later collection by recycling contractors;*
- e. *Segregation and storage of constituents of C&D materials in appropriate containers, skips or stockpiles to enhance the opportunity for reuse and recycling of materials or their proper disposal. Sufficient protective measures provided in the storage area for sorting to avoid damage or contamination;*
- f. *Collection of aluminum cans, paper waste and plastic bottles by site staff, and provision of separately labeled bins to segregate these wastes from other general refuse arising from the work force;*
- g. *Provision of a designated waste working team to collect the refuse on site regularly;*
- h. *Removal of all other un-reusable C&D materials off site as soon as practicable in order to optimize the use of the on-site storage space;*
- i. *Implementation of the trip-ticket system to ensure that the dumping / filling location is used so as to prevent fly tipping. The security guard will ensure only dump trucks with properly completed trip-tickets can leave the site. Wherever practicable, weighing equipment will be provided at the site entrance to accurately record the amount of C&D materials transported off site. The trip-tickets, with valid stamp from an agreed dumping / filling location, will be collected upon return and appropriately filed in the site records;*
- j. *During the storage and transportation of waste, a tarpaulin covering or enclosed containers will be used to minimize fugitive dust emission;*
- k. *Unused chemicals or those with remaining functional capacity will be retained for reuse. The chemicals will be separated for special handling and appropriate treatment at the Chemical Waste Treatment Facilities (CWTF);*
- l. *The setting up of special control measures to regulate storage, labeling, transport and the disposal of classified chemical waste such as paint residues, lubricants or other oil waste including the registration as a chemical waste producer and the disposal of such wastes by a licensed collector to CWTF; and*
- m. *The amount of waste reused, recycled or disposed will be recorded regularly.*

4.4 Handling of C&D Materials

Storage, collection and transportation of the C&D material will be carefully planned and implemented to minimize any adverse impact upon the environment. The generated C&D material will be sorted on site and C&D waste for recycling as appropriate in accordance with ETWB TCW No. 15/2003, or subsequent disposal at approved strategic landfills and Public Filling Areas (PFAs). Wherever practicable, SA/DSA will arrange the segregation of these wastes on site in order to maximize the recovery of reusable and recyclable materials. Separate areas will be designated for segregation and storage where site-specific conditions allow.

The segregated types of C&D materials will be stored in separate covered storage areas to avoid possible cross contamination and loss due to windblown and fugitive dust. If the C&D materials are to be temporarily stored in piles on site, they will either be covered with a tarpaulin or watered regularly to prevent the emission of fugitive dust. SA/DSA will ensure that C&D materials are removed from their origin and processed at designated points in a timely manner.

Recyclable materials such as steel mesh, reinforcement bars, window frames, railing, banisters, and wooden planks will be separated from other C&D materials. These materials will be either reused on site or collected by an external licensed waste recycling agent. If an external recycling agent is required, details of the nominated company will be submitted to the Engineer's Representative.

4.4.1 Waste Sorting

Sufficient space will be provided to accommodate the separation of inert and non-inert materials and a unique access checkpoint with security control. The SM will manage the waste sorting facilities and promptly remove all the sorted and processed materials arising from or in connection with the works from the site to minimize the extent of temporary stockpiling on the site. The categories of C&D materials to be sorted within the waste sorting facilities include:

- Inert materials consisting of earth, building debris, rock fragments, concrete bricks, tiles, masonry and mortar etc;
- Metals;
- Paper/Cardboards; and,
- Timber.

Following the sorting of these wastes, they will be sent separately for reuse and recycling, processing or disposed of as described in the following sections.

Other than large waste sorting facilities, CSAJV will provide refuse and recycling bins respectively to collect different types of refuse generated by the site office and the workforce. These will include bins to collect general refuse such as food waste and recycling bins to collect waste paper separately, plastic bottles and aluminum cans. These bins will be provided in common areas where the wastes are commonly generated such as site offices, workshops, canteen and other site accommodation areas for the workers.

(1) Inert C&D Materials

Following waste sorting, the remaining inert C&D materials will be managed as follows:

Excess Excavated Material

In order to minimize the amount of excess excavated material to be delivered to public fill facilities, the priority for the management options of excess excavated material will be as followings: -

- a. *Suitable excavated material will be stored for backfilling purposes;*
- b. *Excessive excavated material will be transported to other sites for reuse as approved by the Engineer's Representative; and*
- c. *Only the amount of excavated material remaining after reuse as described under Items a. and b. will be transported to the public fill facilities.*

Inert C&D materials which are to be disposed to public filling outlets will be broken down to a size less than 250mm as according to Dumping License conditions prior to disposal. Wet soil with free water or a liquid content of over 70% and other materials such as marine mud, pond mud, household refuse, plastic, metal, industrial and chemical waste matter etc. will not be loaded into the dump truck. This will be controlled by the GF/SE during the earthwork operations and further verified at the exit checkpoint before the trip ticket is issued for each truck.

Concrete Waste

The surplus concrete after each concrete pour will be used for some minor pre-cast elements where practicable. Dry concrete waste, including broken concrete from demolition works, will be sorted out from the other wastes for reuse in site temporary road construction.

All the remaining inert C&D materials will be transported to the public filling facilities approved by Engineer. The trip ticket system will ensure there is no illegal dumping of the above-mentioned materials.

(2) Non-Inert C&D materials

Timber Waste

As far as possible, CSAJV will avoid, reduce and minimize the use of timber in temporary works construction. Where the timber is used for this purpose or for one process / activity with an estimated quantity exceeding 5m³, CSAJV will submit a method statement to the Engineer's Representative for agreement prior to the commencement of the works.

A description, justification and the estimated quantity for every work process / activity requiring the use of timber for temporary works construction.

Metal Wastes

CSAJV will avoid and reduce metal waste during the design, planning and construction process. Cut metal or steel bar will be considered for re-use in temporary or minor works on site. When metal waste has arisen on site, it will be sorted and collected daily by an

assigned work team and stored in a designated storage area for subsequent use or collection by recycling contractors.

General Refuse and C&D Waste

Un-recyclable, non-inert C&D materials, i.e. C&D wastes, and general refuse, which mainly consists of food waste, aluminum cans and waste paper, will be generated from construction activities, workers and the site office.

The C&D waste will be temporarily stored and containers or skips with openable doors will be provided for temporary waste storage to prevent odour, pest and windblown litter.

Office waste will be reduced through the recycling of paper. Sacks for waste paper and baskets for reusable papers will be provided in the Site office. General refuse including food and domestic waste will be stored in enclosed bins or compaction units separate from the construction and chemical wastes. Lunch boxes, plastic bottles, containers, plastic sheets and foam will be sorted and stored in separately labeled bins for subsequent recycling. Reputable recycle contractors will be employed to collect recyclable materials. The amount of waste to be recycled will be recorded, controlled and monitored through the maintenance of WFT.

The general refuse and the un-recyclable C&D waste will be collected and disposed of on a regular basis to minimize the likelihood of odour, pests and litter. They will be transported and disposed of by a licensed waste hauler. A trip-ticket system to trace the transportation and destination of the waste will be implemented and the burning of refuse on the site will be strictly prohibited.

4.4.2 Chemical Waste

For chemical waste produced by a process, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, a 'Chemical Waste Producer' registration will be made with EPD.

Chemical wastes are likely to be generated during maintenance of plant and equipment and these may include spent filter cartridges containing heavy metals, asbestos waste, spent batteries, used mechanical oil, cleaning fluid, spent solvents, lubricating oil and paints and paint containers.

All chemical wastes generated on site will be stored and labeled in accordance with the Code of Practice on the Packaging, Labeling and Storage of Chemical Waste published by EPD. All workers involved in the handling of chemical waste will be trained properly and will be provided with appropriate protective clothing.

The sorting and segregation of chemical waste will be carried out on site to ensure the waste is appropriately handled, labeled and treated prior to disposal off-site. The recoverable chemical wastes such as oil, paint and solvent, will be separated from other chemical wastes and an EPD licensed chemical waste collector will be employed to collect the chemical waste.

Storage of Chemical Waste

Chemical waste will be stored at designated storage areas in accordance with the Code of Practice on the Packaging, Labeling and Storage of Chemical Waste. The containers to be used for the storage of chemical waste will:

- a. *be suitable for the substance they are holding, resistant to corrosion and be maintained in a good condition and kept securely closed;*
- b. *have a capacity of less than 450 L unless the specifications have been approved by the EPD; and,*
- c. *display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations.*

The storage area for chemical waste will:

- a. *be clearly labeled and used solely for the storage of chemical waste;*
- b. *be enclosed on at least three sides;*
- c. *have an impermeable floor and be bunded to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is greater;*
- d. *have adequate ventilation;*
- e. *be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste if necessary); and*
- f. *be arranged so that incompatible materials are adequately separated.*

Disposal of Chemical Waste

A licensed waste collector will be employed to deliver the chemical waste to legal treatment facilities. Waste dry battery will be disposed to SENT landfill while Waste Oil will be transported to Dunwell Industrial (Holdings) Limited for handling purpose. The trip-ticket system will be strictly implemented to ensure the chemical waste is transported by and to proper agents. Trip tickets issued for every chemical waste collection will be retained and filed for future reference and inspection.

Please refer to Section 5.2 for the recording system of C&D material and waste. A sample of the Monthly Waste Flow Table and Record of Timber Usage is given at **Appendix E**.

4.5 Promotion and Training on Waste Management

4.5.1 Environmental Training

The EO and ES are responsible for carrying out the environmental training on waste management. They will analyze the problem and the detailed need of waste management training for the employees, consult with their departmental managers, and seek advice from the senior management.

The environmental training plan shall be reviewed quarterly by the EO in consultation with the Site Agent to identify and review training needs of the construction activities and to introduce new training program.

Site Specific Induction Training

The site specific induction Training cover environmental and waste management in addition to safety will be conducted for all staff and workers employed for the Works or in connection with the Contract. The training content should cover subjects such as organization structure, duties and responsibilities, measures, targets, in-house rules and regulations.

Tool box talk

Workers will receive environmental toolbox talks conducted by the respective front line Supervisors, EO/ES. The toolbox talks will focus on different trade and activities and enhance environmental awareness amongst operatives.

4.5.2 Environmental Promotion

Environmental information

- Display and update appropriate Environmental Signs/Posters at the site entrances and relative works area.
- Environmental news, agenda and minutes of Site Safety Environmental Committee Meeting, emergency, environmental promotion activities will display on site safety bulletin board
- Daily Morning Briefing is an individual workforce gathering in the morning assembly prior to work start to be conducted by the supervisor or gangers. Daily morning briefing will deliver environmental messages, environmental hazards identified and environmental pollution precaution measures to workforce.

Environmental Award

The "Safety and Environmental Star – Worker Award" would be held to promote safety and environmental awareness of individual worker. The performance of the worker on waste management would also be reviewed. The assessment criteria will be based on observation by EO/ES, area foremen report and recommendation from their direct employer and written assessment of safety and environmental knowledge.

5.0 TRIP TICKET SYSTEM AND RECORDING

5.1 Trip Ticket System (TTS)

For the transportation of public fill and C&D wastes, CSAJV will implement and comply with the requirements of the Trip-Ticket System (TTS) stipulated in Works Bureau Technical Circular No. 31/2004. A standalone Site Management Plan for implementation of TTS will be established which should be reviewed and updated on monthly basis.

The manpower resources for TTS

- (1) A senior staff member (with at least two-year experience in site management) fully responsible for implementing and overseeing the operation of the TTS; and
- (2) Experienced person(s) to man each exit from the Site for the purpose of checking every truck carrying C&D materials leaving the Site so as to ensure that the truck driver bears a duly completed, signed and stamped Disposal Delivery Form (DDF).

General Procedure of the TTS

The procedures for implementation of the TTS are as follows:-

- (1) The Site Supervisory Staff will prepare and hand the DDF to the CSAJV on the day of disposal.
- (2) For each truckload of C&D materials leaving the Site, the CSAJV's truck driver must bear a duly completed, signed and stamped DDF.
- (3) For each vehicular trip, CSAJV will present to the operator of the Designed Public Filling Facility / Landfill (operator) the stamped Form prior to disposal of the C&D materials. Upon completion of the disposal, CSAJV will ask the operator for a stamp on the Form together with a computer print-out receipt to acknowledge the disposal. CSAJV will collect and verify the returned Form and computer receipt. A copy of the Form and computer receipt will be maintained by CSAJV for record.
- (4) CSAJV will also present valid "CHIT" in addition to the DDF under the TTS when disposing of construction waste at the waste disposal facilities, as the requirement under the Construction Waste Disposal Charging Scheme.
- (5) CSAJV will maintain a daily record of disposal of C&D materials from the Site including details of the C&D materials, the truck number, departure time, etc., using the Daily Record Summary (DRS).
- (6) CSAJV will submit the duly completed Part 1 of the DRS form promptly to the Site Supervisory Staff by 1:00 pm of the working day following the date of disposal.
- (7) For disposal at government disposal facilities, CSAJV will check the information recorded in the DRS against available information including his own records and data from CEDD's website [<http://www.cedd.gov.hk/eng/services/tripticket/index.html>] and then complete Part 2 of the DRS form for submission to Site Supervisory Staff within 3 working days after the date of disposal.
- (8) ER may request and obtain information from the operator of the Designed Public Filling Facility / Landfill to verify the receipt of the C&D materials and the accuracy of the information on the receipt.

Informing the Truck Drivers

CSAJV will write to all truck drivers whom he has engaged for removal of C&D materials from the Site and draw their attention to the following particular points:

- (a) Each truck carrying C&D materials leaving the Site for a disposal ground must bear a duly completed and stamped DDF, irrespective of the location and nature of the disposal ground.
- (b) The C&D materials must be disposed of at the disposal grounds as stipulated in the DDF.
- (c) What constitutes an improper disposal and that the Public Fill Committee (PFC) will consider revoking the Dumping License from the holder of the offending trucks.
- (d) Truck drivers must bear a valid Dumping License which he can apply from the Civil Engineering and Development Department (CEDD).

A sample of the "CHIT", stamped Disposal Delivery Form (DDF) and Daily Summary Table (DRS) is given at **Appendix F**.

5.2 Waste Recording System

CSAJV will record the quantities of C&D materials generated each month, using the monthly summary "Waste Flow Table" (WFT) CSAJV shall complete the monthly summary WFT.

The following records will be kept by CSAJV for inspection and reporting as necessary by the Environmental Team or the Engineer's Representative:

- Waste disposal permits or licenses
- Record of trip tickets for C&DM disposed off-site
- Record of trip tickets for chemical waste disposed off-site
- Record of non-compliance of the WMP
- Record of corrective action taken to rectify any non-compliance

5.3 Control of Overloading of Dump Trucks

Photo record will be taken for all dump truck before uploading of C&D material and leaving the Site. CSAJV would coordinate with the contractor of DSD Contract no. DC/2009/05 for using their weighbridge as overloading control. All loaded dump trucks will be weighted at the weighbridge prior to issuing trip ticket and leaving the site. The system of overloading control system will be reviewed periodically.

6.0 EVENT CONTINGENCY PLAN FOR NON-COMPLIANCE AND COMPLAINT

6.1 Handling Procedure for Non-compliance and Complaint

A Contingency Group will be set up to respond to non-compliance and complaints on waste management and other environmental issues.

In the Event of Non-Compliance:

1. If any non-compliance is observed during site inspection by DSD, the EO/ES will raise a Corrective & Preventive Action Report (CPAR) to SA/CMs.;
2. The CMs will notify and liaise with the SA of non-compliance to obtain proposals and a response to the CPAR;
3. The EO will notify SA if the non-compliance is an exceedance of the stipulated requirements. In such cases, a copy of the CPAR will be issued to the DSD as a Notification of Non-compliance (NNC);
4. After receipt of the NNC, the SA will propose corrective actions for the non-compliance in line with the JV's CPAR and implement the proposed corrective actions once they have been agreed by DSD;
5. If the implementation of the corrective actions is satisfactory, the non-compliance record (CPAR) will be closed and the DSD advised accordingly;
6. The CMs/EO will propose preventive actions within 3 working days if it has not been already included within the JV's response after the closure of the non-compliance records; and
7. The SA/CMs/EO will record CPARs accordingly in the CPAR logsheet.
8. Environmental Team and Engineer representative should be notified immediately in case of the event of non-compliance.

In the Event of Complaint

1. Complaint related to environmental management will be collected by the EO/ES. The complaint will be referred to the SA/CMs for carrying out complaint investigation procedures;
2. The SA/CMs will log complaint and date of receipt onto the complaint database and inform the SM, the DSD immediately within 2 working day;
3. Within 2 working day after receipt of the notification of complaint, the EO/ES will identify the source of the problem and provide the DSD relevant works site information, e.g. types and locations of construction works;
4. If the complaint is valid and due to project works, the EO/ES will liaise with SA/CMs to propose corrective actions/mitigation measures to DSD. The SA/CMs will implement the mitigation measures once they have been agreed;
5. The EO/ES will report the investigation results and subsequent actions taken, to the DSD after the implementation of mitigation measures; and
6. If no further comments or complaints are received from the complainant within 20 days after responding to the complainant, close the complaint record.
7. Environmental Team and Engineer representative should be notified immediately in case of the event of complaint.

6.2 Environmental Emergency Procedures for Chemical Spillage

For any environmental emergency involving the spillage or leakage of chemicals, CSAJV will implement the following response procedures.

- *Instruct untrained personnel to keep at a safe distance well away from the spillage area;*
- *If the spillage is in an enclosed area (e.g. inside the chemical storage area), open the doors and windows to enhance ventilation;*
- *If the spillage involves highly toxic, volatile or hazardous materials, initiate emergency evacuation (refer to the Construction Safety Plan) and call the emergency service;*
- *Only persons equipped with suitable protective clothing and equipment will be allowed to enter and clean up the chemical spillage area;*
- *Spillage of liquid at storage area - Where the spillage is contained in the enclosed storage area, the liquid will be transferred into suitable chemical waste containers by suitable handheld equipment, such as hand operated pumps, scoops and shovel. If the spillage quantity is small, it will be covered and mixed with suitable absorbing materials such as tissue paper, dry soft sand or vermiculite. The resultant slurry will be treated as chemical waste and transferred to suitable containers for disposal;*
- *Spillage at other areas - For spillage in other areas, immediate action is required to contain the spillage. Suitable liquid absorbing materials such as tissue paper, dry soft sand or vermiculite will be used to cover the spill. The resultant slurry will be treated as chemical waste and transferred into containers for proper disposal; and*
- *In incidents where the spillage may result in significant contamination of an area or risk of pollution, the EPD will be informed immediately.*

The communication channel / reporting procedure for emergency event and chemical spillage on site

- *An effective communication system through telephone will establish and maintain to allow instant contact between site supervisory staff, environmental officer, environmental supervisors, first-aiders and all subcontractors*
- *An emergency telephone list which includes the off duty telephone numbers of the key staff and relevant government departments will be displayed on site notice board.*
- *The environmental officer is acted as the public relation officer to handle public complaint such as noise, dust, waste water etc. and liaise with the government department such as Environmental Protection Department and Food & Environmental Hygiene Department.*
- *The external communication system shall be reviewed for adequacy at least annually and whenever major or high-potential accidents or incidents occur which identify external communications as a basic cause.*

7.0 AUDITING PROPOSAL

General Foreman and EO/ES will conduct weekly site inspections to ensure this WMP is properly followed. In addition to internal audit will be performed to review the effectiveness on the implementation of this WMP:-


- Internal audits will be performed in line with the WMP by an environmental auditor with well experienced personnel
- Audits will be planned to by Environmental Officer determine when and where to audits which are scheduled on the basis of the status and importance of the activity
- Audit comprises of document review, site inspection and discussion with responsible person, so as to address all key elements of the WMP and implementation of procedures and maintenance of records
- Environmental and Safety Officer will monitor the status of completion of the follow-up action programme after internal auditing
- Result of audits will be taken into account for management review for reviewing the implementation status and the effectiveness of the audit system

The waste (generated from construction activities) handling procedures documented in this stand-alone WMP will be incorporated as Section 7.0 of Environmental Management Plan and the effectiveness of waste management and implementation of trip ticket system will be discussed and reviewed during the SSEMC and SSEC meetings on monthly basis.

Appendix A

Project Environmental Organization Chart for Waste Management

Appendix A Environmental Organization Chart of Key Personnel

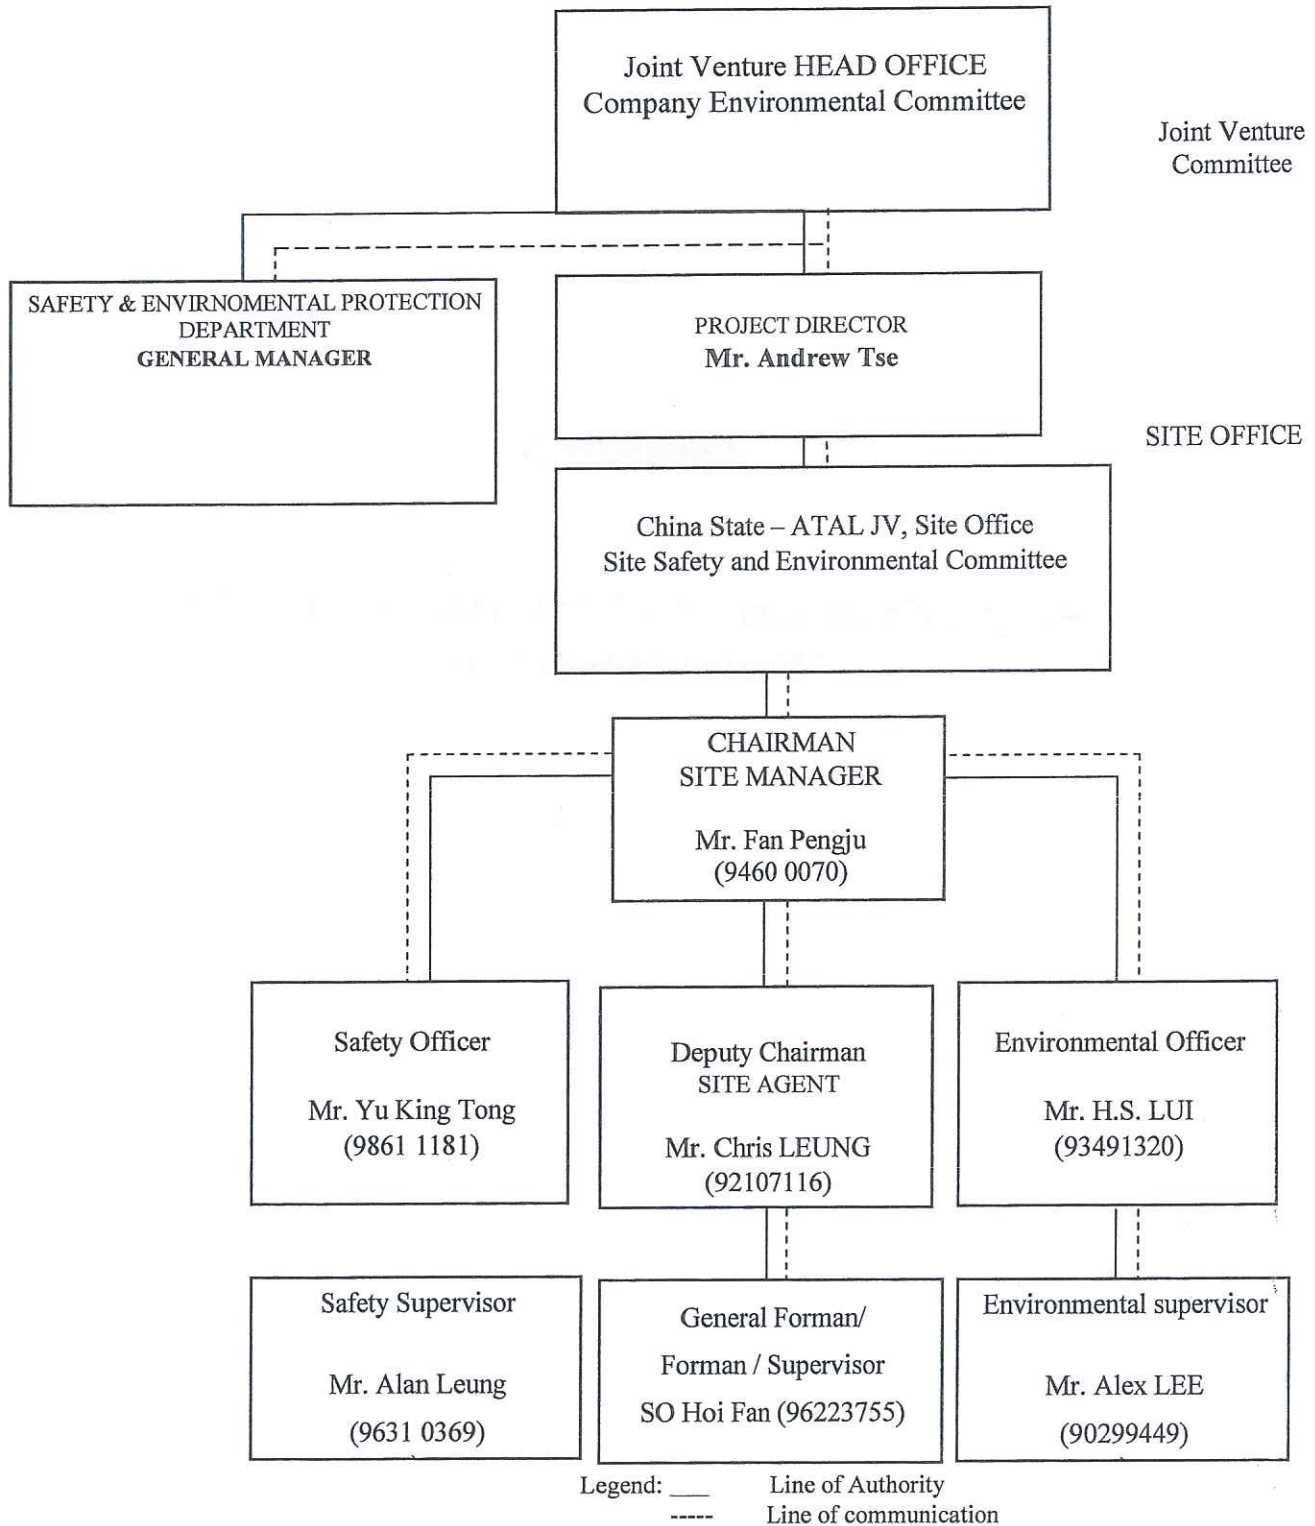

Appendix B

Tentative C&D Material Generation Programme (Monthly Schedule)

DC/2009/17 Harbour Area Treatment Scheme Stage 2A - Upgrading Works at Stonecutters Island Sewage Treatment Works
Sludge Dewatering Facilities
C&DMMP (as at end October 2010)

Latest Programme for Generation & Import of Materials in each Reporting Period	Programmed Quantity for Generation of Surplus C&D Materials					Programmed Quantity for Imported of Fill		
	Inert C&D Materials (Soft Public Fill)	Good Quality Rock (with breakdown)	Broken Concrete	Marine Deposit	C&D Waste	Inert C&D Materials (Soft Public Fill)	Rock	Sand Fill
Unit	(m3)	(m3)	(m3)	(m3)	(m3)	(m3)	(m3)	(m3)
2010/07 (Actual)								
2010/08 (Actual)	0	0	0	0	0			
2010/09 (Actual)	0	0	0	0	0			
2010/10 (Actual)	0	0	0	0	0			
2010/11 (Forecast)	33	0	0	0	12			
2010/12 (Forecast)	337	0	0	0	12			
Sub-total	370	0	0	0	24	0	0	0
2011/01 (Forecast)	611	0	0	0	12			
2011/02 (Forecast)	611	0	0	0	12			
2011/03 (Forecast)	611	0	0	0	12			
2011/04 (Forecast)	611	0	0	0	10			
2011/05 (Forecast)	611	0	0	0	10			
2011/06 (Forecast)	611	0	0	0	10			
Sub-total	3666	0	0	0	66	0	0	0
2011/07 (Forecast)	370	0	0	0	10			
2011/08 (Forecast)	370	0	0	0	7			
2011/09 (Forecast)	370	0	0	0	7			
2011/10 (Forecast)	370	0	0	0	7			
2011/11 (Forecast)	182	0	0	0	7			
2011/12 (Forecast)	182	0	0	0	7			
Sub-total	1844	0	0	0	45	0	0	0
Year 2010 to 2011, Total	5880	0	0	0	135	0	0	0
2012/01 (Forecast)	182	0	0	0	7			
2012/02 (Forecast)	182	0	0	0	7			
2012/03 (Forecast)	182	0	0	0	7			
2012/04 (Forecast)	182	0	0	0	7			
2012/05 (Forecast)	182	0	0	0	7			
2012/06 (Forecast)	0	0	0	0	7			
Sub-total	910	0	0	0	42	0	0	0
2012/07 (Forecast)	8	0	0	0	7			
2012/08 (Forecast)	8	0	0	0	7			
2012/09 (Forecast)	8	0	0	0	7			
2012/10 (Forecast)	8	0	0	0	6			
2012/11 (Forecast)	8	0	0	0	6			
2012/12 (Forecast)	8	0	0	0	6			
Sub-total	48	0	0	0	39	0	0	0
2013/01 (Forecast)	8	0	0	0	6			
2013/02 (Forecast)	8	0	0	0	6			
2013/03 (Forecast)	8	0	0	0	6			
2013/04 (Forecast)	8	0	0	0	10			
2013/05 (Forecast)	8	0	0	0	10			
2013/06 (Forecast)	8	0	0	0	10			
Sub-total	48	0	0	0	48	0	0	0
2013/07 (Forecast)	8	0	0	0	16			
2013/08 (Forecast)	8	0	0	0	16			
2013/09 (Forecast)	8	0	0	0	16			
2013/10 (Forecast)	8	0	230	0	16			
2013/11 (Forecast)	8	0	230	0	16			
2013/12 (Forecast)	8	0	230	0	16			
Sub-total	48	0	690	0	96	0	0	0
Year 2012 to 2013, Total	1054	0	690	0	225	0	0	0
2014/01 (Forecast)	8	0	230	0	16			
2014/02 (Forecast)	8	0	230	0	16			
2014/03 (Forecast)	8	0	230	0	16			
2014/04 (Forecast)	8	0	170	0	14			
2014/05 (Forecast)	79	0	170	0	14			
2014/06 (Forecast)	79	0	170	0	14			

[illegible]


DC/2009/17 Harbour Area Treatment Scheme Stage 2A - Upgrading Works at Stonecutters Island Sewage Treatment Works
Sludge Dewatering Facilities
C&DMMP (as at end October 2010)

Latest Programme for Generation & Import of Materials in each Reporting Period	Programmed Quantity for Generation of Surplus C&D Materials					Programmed Quantity for Imported of Fill		
	Inert C&D Materials (Soft Public Fill)	Good Quality Rock (with breakdown)	Broken Concrete	Marine Deposit	C&D Waste	Inert C&D Materials (Soft Public Fill)	Rock	Sand Fill
Density (t/m ³)	2.00	2.50	2.50	2.00	1.00	1.80	2.00	1.90
	(t)	(t)	(t)	(t)	(t)	(t)	(t)	(t)
2010/07 (Actual)								
2010/08 (Actual)								
2010/09 (Actual)								
2010/10 (Forecast)								
2010/11 (Forecast)	66	0	0	0	12			
2010/12 (Forecast)	674	0	0	0	12			
Sub-total	740	0	0	0	24	0	0	0
2011/01 (Forecast)	1222	0	0	0	12			
2011/02 (Forecast)	1222	0	0	0	12			
2011/03 (Forecast)	1222	0	0	0	12			
2011/04 (Forecast)	1222	0	0	0	10			
2011/05 (Forecast)	1222	0	0	0	10			
2011/06 (Forecast)	1222	0	0	0	10			
Sub-total	7332	0	0	0	66	0	0	0
2011/07 (Forecast)	740	0	0	0	10			
2011/08 (Forecast)	740	0	0	0	7			
2011/09 (Forecast)	740	0	0	0	7			
2011/10 (Forecast)	740	0	0	0	7			
2011/11 (Forecast)	364	0	0	0	7			
2011/12 (Forecast)	364	0	0	0	7			
Sub-total	3688	0	0	0	45	0	0	0
Page Total	11760	0	0	0	135	0	0	0
2012/01 (Forecast)	364	0	0	0	7			
2012/02 (Forecast)	364	0	0	0	7			
2012/03 (Forecast)	364	0	0	0	7			
2012/04 (Forecast)	364	0	0	0	7			
2012/05 (Forecast)	364	0	0	0	7			
2012/06 (Forecast)	0	0	0	0	7			
Sub-total	1820	0	0	0	42	0	0	0
2012/07 (Forecast)	16	0	0	0	7			
2012/08 (Forecast)	16	0	0	0	7			
2012/09 (Forecast)	16	0	0	0	7			
2012/10 (Forecast)	16	0	0	0	6			
2012/11 (Forecast)	16	0	0	0	6			
2012/12 (Forecast)	16	0	0	0	6			
Sub-total	96	0	0	0	39	0	0	0
2013/01 (Forecast)	16	0	0	0	6			
2013/02 (Forecast)	16	0	0	0	6			
2013/03 (Forecast)	16	0	0	0	6			
2013/04 (Forecast)	16	0	0	0	10			
2013/05 (Forecast)	16	0	0	0	10			
2013/06 (Forecast)	16	0	0	0	10			
Sub-total	96	0	0	0	48	0	0	0
2013/07 (Forecast)	16	0	0	0	16			
2013/08 (Forecast)	16	0	0	0	16			
2013/09 (Forecast)	16	0	0	0	16			
2013/10 (Forecast)	16	0	575	0	16			
2013/11 (Forecast)	16	0	575	0	16			
2013/12 (Forecast)	16	0	575	0	16			
Sub-total	96	0	1725	0	96	0	0	0
Page Total	2108	0	1725	0	225	0	0	0
2014/01 (Forecast)	16	0	575	0	16			
2014/02 (Forecast)	16	0	575	0	16			
2014/03 (Forecast)	16	0	575	0	16			
2014/04 (Forecast)	16	0	425	0	14			
2014/05 (Forecast)	158	0	425	0	14			

Latest Programme for Generation & Import of Materials in each Reporting Period	Programmed Quantity for Generation of Surplus C&D Materials					Programmed Quantity for Imported of Fill		
	Inert C&D Materials (Soft Public Fill)	Good Quality Rock (with breakdown)	Broken Concrete	Marine Deposit	C&D Waste	Inert C&D Materials (Soft Public Fill)	Rock	Sand Fill
Density (t/m ³)	2.00	2.50	2.50	2.00	1.00	1.80	2.00	1.90
2014/06 (Forecast)	158	0	425	0	14			
Sub-total	380	0	3000	0	90	0	0	0
2014/07 (Forecast)	98	0	170	0	10			
2014/08 (Forecast)	140	0	168	0	10			
2014/09 (Forecast)	846	0	168	0	10			
2014/10 (Forecast)	846	0	0	0	10			
2014/11 (Forecast)	846	0	0	0	8			
2014/12 (Forecast)	846	0	0	0	8			
Sub-total	3622	0	505	0	56	0	0	0
2015/01 (Forecast)	964	0	0	0	8			
2015/02 (Forecast)	1032	0	0	0	0			
2015/03 (Forecast)	1464	0	0	0	0			
2015/04 (Forecast)	296	0	0	0	0			
2015/05 (Forecast)	296	0	0	0	0			
2015/06 (Forecast)	66	0	0	0	0			
Sub-total	4118	0	0	0	8	0	0	0
2015/07 (Forecast)	66	0	0	0	0			
2015/08 (Forecast)	66	0	0	0	0			
2015/09 (Forecast)	0	0	0	0	0			
2015/10 (Forecast)	0	0	0	0	0			
2015/11 (Forecast)	0	0	0	0	0			
2015/12 (Forecast)	0	0	0	0	0			
Sub-total	132	0	0	0	0	0	0	0
Page Total	8252	0	3505	0	154	0	0	0
2016/01 (Forecast)	0	0	0	0	0			
2016/02 (Forecast)	0	0	0	0	0			
2016/03 (Forecast)	0	0	0	0	0			
2016/04 (Forecast)	0	0	0	0	0			
2016/05 (Forecast)	0	0	0	0	0			
2016/06 (Forecast)	0	0	0	0	0			
Sub-total	0	0	0	0	0	0	0	0
2016/07 (Forecast)	0	0	0	0	0			
2016/08 (Forecast)	0	0	0	0	0			
2016/09 (Forecast)	0	0	0	0	0			
2016/10 (Forecast)	0	0	0	0	0			
2016/11 (Forecast)	0	0	0	0	0			
2016/12 (Forecast)	0	0	0	0	0			
Sub-total	0	0	0	0	0	0	0	0
Page Total	0	0	0	0	0	0	0	0
Overall Total (t)	22120	0	5230	0	514	0	0	0
Overall Total (m ³)	11060	0	2092	0	514	0	0	0

Appendix C

General Layout Plan for On Site Waste Management

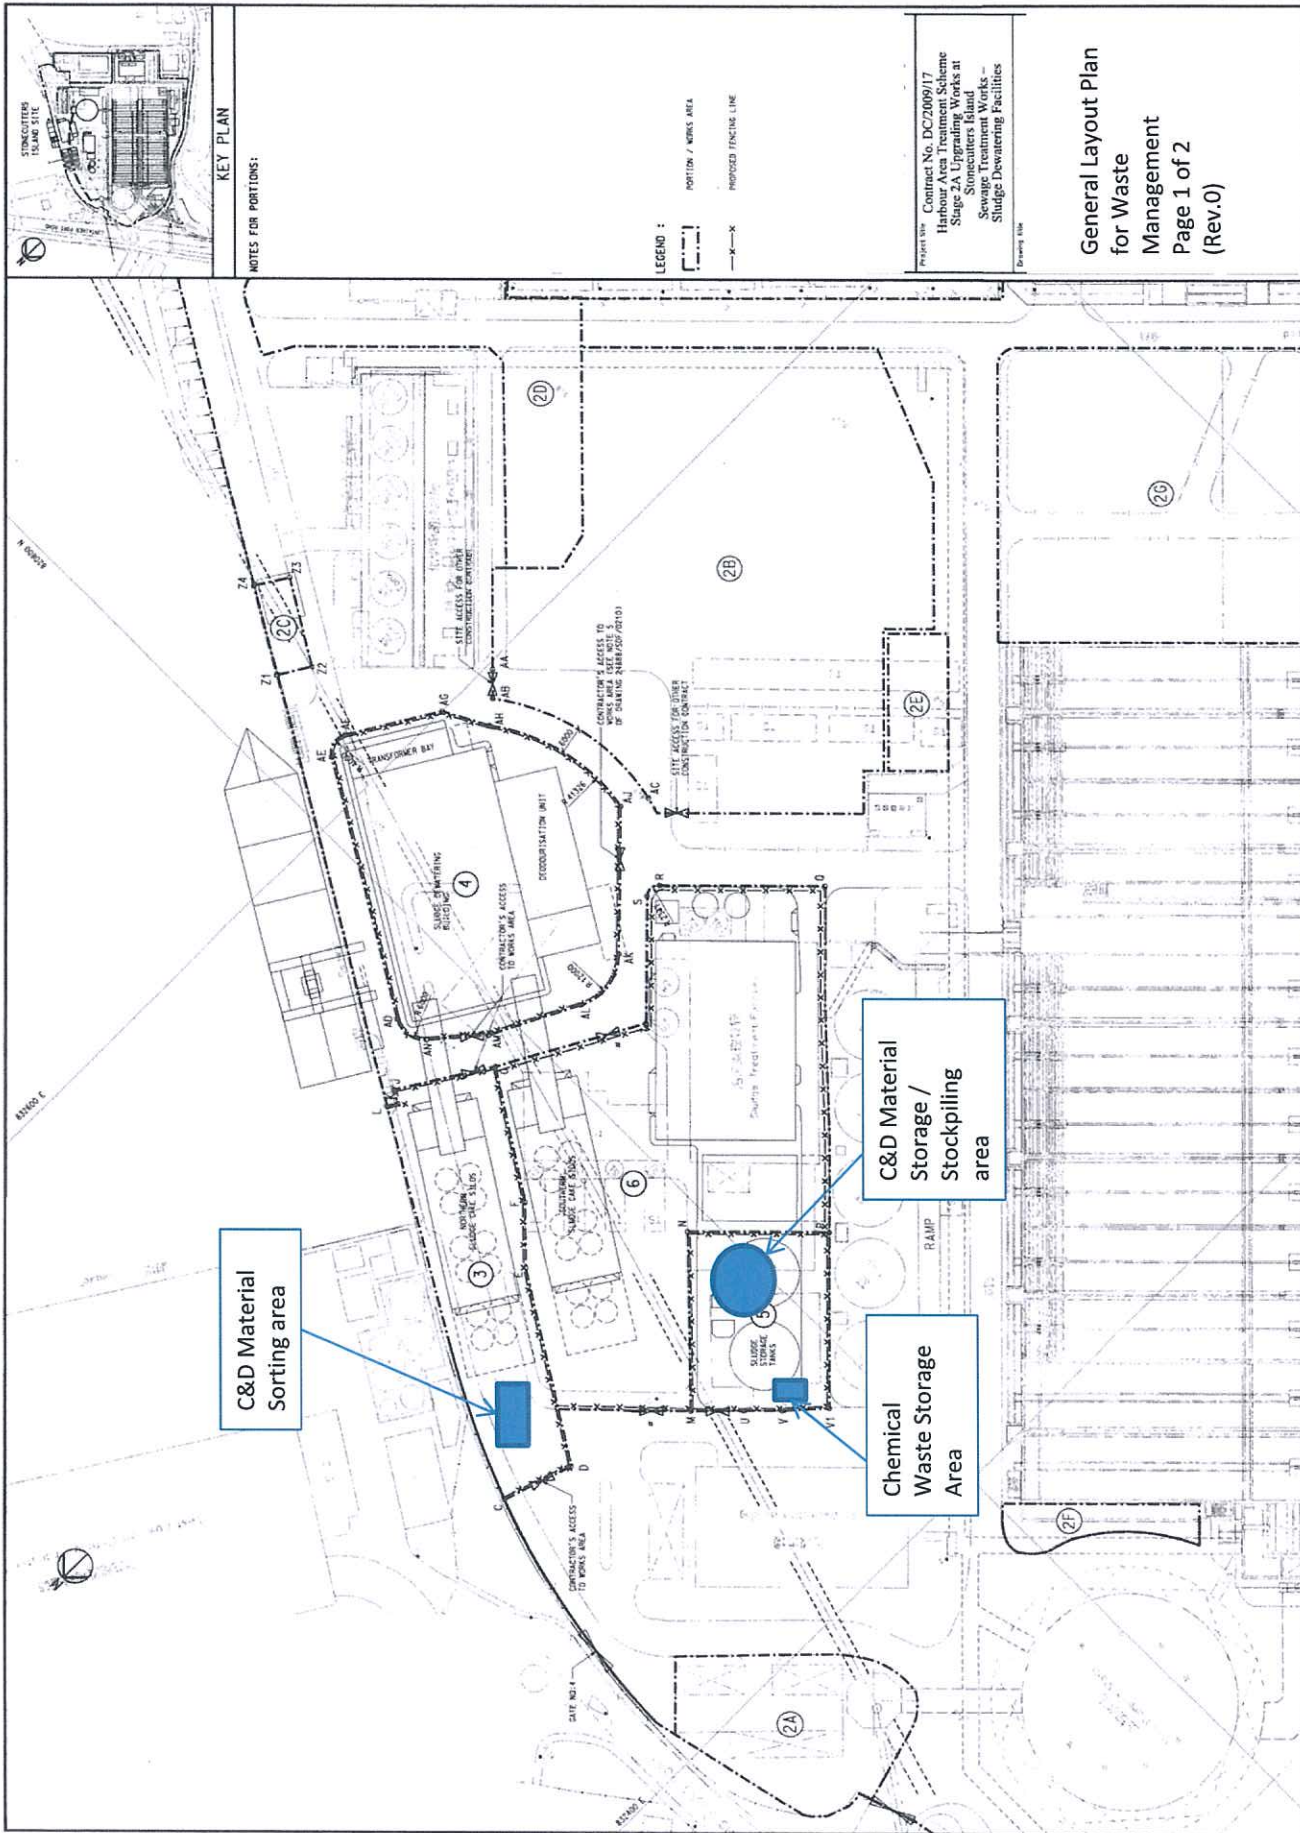

Appendix D

Waste Classification and their Recommended Usage / Outlet

DSD Contract No. DC/200917
Habour Area Treatment Scheme Stage 2A
Upgrading Works at Stonecutters Island Sewage Treatment Works
– Sludge Dewatering Facilities

Waste Stream	Waste Type	Recommended Usage/Outlet
Inert Materials to Public Fill	<ul style="list-style-type: none"> Aggregate, debris, soil and concrete Excavated and Fill Materials 	<ul style="list-style-type: none"> On-site reuse whenever possible Re-process as construction materials Reclamation and site formation at Public Filling Areas
Non-inert Materials (less than 30% by weight of inert material) to Landfill	<ul style="list-style-type: none"> Bamboo, timber, plants, packaging waste and other organic waste Metal (including steel mesh, reinforcement bars, window frames, railings, banisters, etc.) Glass Plastic, Rubber Expanded polystyrene 	<ul style="list-style-type: none"> Selectively segregate for reuse or recycling Timber over specific length shall be used as much as practicable Licensed steel mills in Hong Kong or approved overseas steel mills for re-processing for metal products Substitute for sand and aggregates as pipe-bedding material, gravel backfill for walls, crushed stone surfacing, backfill and bedding Synthetic materials in form of plastic lumber for landscaping, horticulture and hydraulic engineering Manufacture of rubber slate tile use in roofing and sport / playground surface mat Manufacture of lightweight concrete for non-structural works
Special Waste	<ul style="list-style-type: none"> Chemical Waste (defined under Schedule 1 of the Waste Disposal (Chemical Waste) Regulations) Asbestos Contaminated soil 	<ul style="list-style-type: none"> Chemical Waste Treatment Centre or other facilities licensed by EPD (Environmental Protection Department) Gazette hazardous waste disposal site Gazette disposal site for contaminated soil
General Refuse	<ul style="list-style-type: none"> Paper, cardboard, aluminum cans, plastic bottles 	<ul style="list-style-type: none"> Selectively segregate for recycling Dispose at refuse transfer stations

Appendix E

Monthly Summary of Waste Flow Table & Record of Timber Usage

MONTHLY SUMMARY WASTE FLOW TABLE

Name of Department :

Contract No.: DC/2009/17

Monthly summary waste Flow Table for 2010 (year)

Date	Actual Quantities of Inert C & D Materials Generated Monthly							Actual Quantities of non-inert C & D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete (see Note 5)	Soil/Slurry (see Note 5)	Reused in the contract	Reused in other Projects on site	Disposed to Public Fill	Imported Fill	Metals	Paper cardboard packaging	Plastics (see Note 3)	Chemical wastes	Others e.g. General refuses
Jan-10	(in Ton)	(in Ton)	(in Ton)	(in m ³)	(in m ³)	(in m ³)	(in '000m ³)	(in Ton)	(in '000kg)	(in '000kg)	(in 'L)	(in 'TON)
Feb-10												
Mar-10												
Apr-10												
May-10												
Jun-10												
July-10												
August-10	0	0	0	0	0	0	0	0	0	0	0	0
September-10	0	0	0	0	0	0	0	0	0	0	0	0
October-10												
November-10												
December-10												
Total	0	0	0	0	0	0	0	0	0	0	0	0

Forecast of Total quantities of C&D Materials to be Genated from the Contract											Forecast of Total quantities of non-inert C&d Materials to be Genated from the Contract			
Total Quantity Generated (inTon)	Hard Rock and Large Broken Concrete (inTon)	Soil/Slurry (inTon)	Reused in the contract (in '000m ³)	Reused in other Projects (in '000m ³)	Disposed to Barging Point (in '000m ³)	Imported Fill (in '000m ³)	Metals (inTon)	Paper cardboard packaging (in '000kg)	Plastics (see Note 3) (in '000kg)	Chemical wastes (in 'L)	Others e.g. General refuses (inTon)			
27350	5230	22,120	-	-	13152	-	812000	1000	2000	492	514			

Notes:

- (1) The performance targets are given in PS Clause 6(14)
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site
- (3) Plastic refer to plastic bottles/containers, Plastic sheets/form from packaging material.
- (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works together with a breakdown of the nature where the total amount of C & D materials expected to be generated from the Works is equal to or exceeding 30,000m (PS Clause 8(4) (to refers))Delete Note (4) and the table above on the foreman where inapplicable.
- (5) The density of Broken Concrete and soil are 2.5 ton/m³ and 2.0 ton/m³ respectively

Appendix D

Waste Classification and their Recommended Usage / Outlet

Waste Stream	Waste Type	Recommended Usage/Outlet
Inert Materials to Public Fill	<ul style="list-style-type: none"> Aggregate, debris, soil and concrete Excavated and Fill Materials 	<ul style="list-style-type: none"> On-site reuse whenever possible Re-process as construction materials Reclamation and site formation at Public Filling Areas
Non-inert Materials (less than 30% by weight of inert material) to Landfill	<ul style="list-style-type: none"> Bamboo, timber, plants, packaging waste and other organic waste Metal (including steel mesh, reinforcement bars, window frames, railings, banisters, etc.) Glass Plastic, Rubber Expanded polystyrene 	<ul style="list-style-type: none"> Selectively segregate for reuse or recycling Timber over specific length shall be used as much as practicable Licensed steel mills in Hong Kong or approved overseas steel mills for re-processing for metal products Substitute for sand and aggregates as pipe-bedding material, gravel backfill for walls, crushed stone surfacing, backfill and bedding Synthetic materials in form of plastic lumber for landscaping, horticulture and hydraulic engineering Manufacture of rubber slate tile use in roofing and sport / playground surface mat Manufacture of lightweight concrete for non-structural works
Special Waste	<ul style="list-style-type: none"> Chemical Waste (defined under Schedule 1 of the Waste Disposal (Chemical Waste) Regulations) Asbestos Contaminated soil 	<ul style="list-style-type: none"> Chemical Waste Treatment Centre or other facilities licensed by EPD (Environmental Protection Department) Gazette hazardous waste disposal site Gazette disposal site for contaminated soil
General Refuse	<ul style="list-style-type: none"> Paper, cardboard, aluminum cans, plastic bottles 	<ul style="list-style-type: none"> Selectively segregate for recycling Dispose at refuse transfer stations

Appendix E

Monthly Summary of Waste Flow Table & Record of Timber Usage

MONTHLY SUMMARY WASTE FLOW TABLE

Name of Department :

Contract No.: DC/2009/17

Monthly summary waste Flow Table for 2010 (year)

Date	Actual Quantities of Inert C & D Materials Generated Monthly							Actual Quantities of non-inert C & D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete (see Note 5)	Soil/Slurry (see Note 5)	Reused in the contract	Reused in other Projects on site	Disposed to Public Fill	Imported Fill	Metals	Paper cardboard packaging	Plastics (see Note 3)	Chemical wastes	Others e.g. General refuses
Jan-10	(in Ton)	(in Ton)	(in Ton)	(in m ³)	(in m ³)	(in m ³)	(in '000m ³)	(in Ton)	(in '000kg)	(in '000kg)	(in 'L)	(in 'TON)
Feb-10												
Mar-10												
Apr-10												
May-10												
Jun-10												
July-10												
August-10	0	0	0	0	0	0	0	0	0	0	0	0
September-10	0	0	0	0	0	0	0	0	0	0	0	0
October-10												
November-10												
December-10												
Total	0	0	0	0	0	0	0	0	0	0	0	0

Forecast of Total quantities of C&D Materials to be Genated from the Contract											Forecast of Total quantities of non-inert C&d Materials to be Genated from the Contract	
Total Quantity Generated	Hard Rock and Large Broken Concrete	Soil/Slurry	Reused in the contract	Reused in other Projects	Disposed to Barging Point	Imported Fill	Metals	Paper cardboard packaging	Plastics (see Note 3)	Chemical wastes	Others e.g. General refuses	
(inTon)	(inTon)	(inTon)	(in '000m³)	(in '000m³)	(in '000m³)	(in '000m³)	(inTon)	(in '000kg)	(in '000kg)	(in 'L)	(inTon)	
27350	5230	22,120	-	-	13152	-	812000	1000	2000	492	514	

Notes:

- (1) The performance targets are given in PS Clause 6(14)
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site
- (3) Plaster, refer to plastic bottles/containers, Plastic sheets/form from packaging material.
- (4) The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works together with a breakdown of the nature where the total amount of C & D materials expected to be generated from the Works is equal to or exceeding 30,000m (PS Clause 8(4) (to refers))Delete Note (4) and the table above on the foreman where inapplicable.
- (5) The density of Broken Concrete and soil are 2.5 ton/m³ and 2.0 ton/m³ respectively

Harbour Area Treatment Scheme Stage 2A
Upgrading Works at Stonecutters Island Sewage Treatment Works -
Sludge Dewatering Facilities

Summary Table for Work Processes or Activities Requiring Timber for Temporary Works

Contract No.: _____ DC/2009/17

Contract Title: Harbour Harbour Area Treatment Scheme Stage 2A Upgrading Works at Stonecutters Island Sewage Treatment Works

— Sludge Dewatering Facilities.....

Item No.	Description of Works Process or Activity [see note (a) below]	Justifications for Using Timber in Temporary Construction Works	Est. Quantities of Timber Used (m ³)	Actual Quantities used (m ³)	Remarks
1.					
2.					
3.					
4.					
5.					
6.					
7.					
8.					
Total Estimated Quantity of Timber Used					

- Notes:
- (a) The Contractor shall list out all the work items requiring timber for use in temporary construction works. Several minor work items may be grouped into one for ease of updating.
 - (b) The summary table shall be submitted to the Engineer's Representative monthly together with the Waste Flow Table for review and monitoring in accordance with the PS Clause 25.40(5).

Appendix F

Sample of CHIT, Disposal Delivery Form & Daily Summary Record

THE UNIVERSITY OF CHICAGO PRESS
50 EAST LAKE STREET, CHICAGO, ILL. 60601-3043
TEL: (773) 837-3000 FAX: (773) 837-3001
WWW.CHICAGO.PRESS.EDU

1
2
3
4
5
6
7
8
9
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26
27
28
29
30
31
32
33
34
35
36
37
38
39
40
41
42
43
44
45
46
47
48
49
50
51
52
53
54
55
56
57
58
59
60
61
62
63
64
65
66
67
68
69
70
71
72
73
74
75
76
77
78
79
80
81
82
83
84
85
86
87
88
89
90
91
92
93
94
95
96
97
98
99
100

101
102
103
104
105
106
107
108
109
110
111
112
113
114
115
116
117
118
119
120
121
122
123
124
125
126
127
128
129
130
131
132
133
134
135
136
137
138
139
140
141
142
143
144
145
146
147
148
149
150
151
152
153
154
155
156
157
158
159
160
161
162
163
164
165
166
167
168
169
170
171
172
173
174
175
176
177
178
179
180
181
182
183
184
185
186
187
188
189
190
191
192
193
194
195
196
197
198
199
200

201
202
203
204
205
206
207
208
209
210
211
212
213
214
215
216
217
218
219
220
221
222
223
224
225
226
227
228
229
230
231
232
233
234
235
236
237
238
239
240
241
242
243
244
245
246
247
248
249
250
251
252
253
254
255
256
257
258
259
260
261
262
263
264
265
266
267
268
269
270
271
272
273
274
275
276
277
278
279
280
281
282
283
284
285
286
287
288
289
290
291
292
293
294
295
296
297
298
299
300
301
302
303
304
305
306
307
308
309
310
311
312
313
314
315
316
317
318
319
320
321
322
323
324
325
326
327
328
329
330
331
332
333
334
335
336
337
338
339
340
341
342
343
344
345
346
347
348
349
350
351
352
353
354
355
356
357
358
359
360
361
362
363
364
365
366
367
368
369
370
371
372
373
374
375
376
377
378
379
380
381
382
383
384
385
386
387
388
389
390
391
392
393
394
395
396
397
398
399
400
401
402
403
404
405
406
407
408
409
410
411
412
413
414
415
416
417
418
419
420
421
422
423
424
425
426
427
428
429
430
431
432
433
434
435
436
437
438
439
440
441
442
443
444
445
446
447
448
449
450
451
452
453
454
455
456
457
458
459
460
461
462
463
464
465
466
467
468
469
470
471
472
473
474
475
476
477
478
479
480
481
482
483
484
485
486
487
488
489
490
491
492
493
494
495
496
497
498
499
500
501
502
503
504
505
506
507
508
509
510
511
512
513
514
515
516
517
518
519
520
521
522
523
524
525
526
527
528
529
530
531
532
533
534
535
536
537
538
539
540
541
542
543
544
545
546
547
548
549
550
551
552
553
554
555
556
557
558
559
560
561
562
563
564
565
566
567
568
569
570
571
572
573
574
575
576
577
578
579
580
581
582
583
584
585
586
587
588
589
590
591
592
593
594
595
596
597
598
599
600
601
602
603
604
605
606
607
608
609
610
611
612
613
614
615
616
617
618
619
620
621
622
623
624
625
626
627
628
629
630
631
632
633
634
635
636
637
638
639
640
641
642
643
644
645
646
647
648
649
650
651
652
653
654
655
656
657
658
659
660
661
662
663
664
665
666
667
668
669
670
671
672
673
674
675
676
677
678
679
680
681
682
683
684
685
686
687
688
689
690
691
692
693
694
695
696
697
698
699
700
701
702
703
704
705
706
707
708
709
710
711
712
713
714
715
716
717
718
719
720
721
722
723
724
725
726
727
728
729
730
731
732
733
734
735
736
737
738
739
740
741
742
743
744
745
746
747
748
749
750
751
752
753
754
755
756
757
758
759
760
761
762
763
764
765
766
767
768
769
770
771
772
773
774
775
776
777
778
779
780
781
782
783
784
785
786
787
788
789
790
791
792
793
794
795
796
797
798
799
800
801
802
803
804
805
806
807
808
809
810
811
812
813
814
815
816
817
818
819
820
821
822
823
824
825
826
827
828
829
830
831
832
833
834
835
836
837
838
839
840
841
842
843
844
845
846
847
848
849
850
851
852
853
854
855
856
857
858
859
860
861
862
863
864
865
866
867
868
869
870
871
872
873
874
875
876
877
878
879
880
881
882
883
884
885
886
887
888
889
890
891
892
893
894
895
896
897
898
899
900
901
902
903
904
905
906
907
908
909
910
911
912
913
914
915
916
917
918
919
920
921
922
923
924
925
926
927
928
929
930
931
932
933
934
935
936
937
938
939
940
941
942
943
944
945
946
947
948
949
950
951
952
953
954
955
956
957
958
959
960
961
962
963
964
965
966
967
968
969
970
971
972
973
974
975
976
977
978
979
980
981
982
983
984
985
986
987
988
989
990
991
992
993
994
995
996
997
998
999
1000
1001
1002
1003
1004
1005
1006
1007
1008
1009
1010
1011
1012
1013
1014
1015
1016
1017
1018
1019
1020
1021
1022
1023
1024
1025
1026
1027
1028
1029
1030
1031
1032
1033
1034
1035
1036
1037
1038
1039
1040
1041
1042
1043
1044
1045
1046
1047
1048
1049
1050
1051
1052
1053
1054
1055
1056
1057
1058
1059
1060
1061
1062
1063
1064
1065
1066
1067
1068
1069
1070
1071
1072
1073
1074
1075
1076
1077
1078
1079
1080
1081
1082
1083
1084
1085
1086
1087
1088
1089
1090
1091
1092
1093
1094
1095
1096
1097
1098
1099
1100
1101
1102
1103
1104
1105
1106
1107
1108
1109
1110
1111
1112
1113
1114
1115
1116
1117
1118
1119
1120
1121
1122
1123
1124
1125
1126
1127
1128
1129
1130
1131
1132
1133
1134
1135
1136
1137
1138
1139
1140
1141
1142
1143
1144
1145
1146
1147
1148
1149
1150
1151
1152
1153
1154
1155
1156
1157
1158
1159
1160
1161
1162
1163
1164
1165
1166
1167
1168
1169
1170
1171
1172
1173
1174
1175
1176
1177
1178
1179
1180
1181
1182
1183
1184
1185
1186
1187
1188
1189
1190
1191
1192
1193
1194
1195
1196
1197
1198
1199
1200
1201
1202
1203
1204
1205
1206
1207
1208
1209
1210
1211
1212
1213
1214
1215
1216
1217
1218
1219
1220
1221
1222
1223
1224
1225
1226
1227
1228
1229
1230
1231
1232
1233
1234
1235
1236
1237
1238
1239
1240
1241
1242
1243
1244
1245
1246
1247
1248
1249
1250
1251
1252
1253
1254
1255
1256
1257
1258
1259
1260
1261
1262
1263
1264
1265
1266
1267
1268
1269
1270
1271
1272
1273
1274
1275
1276
1277
1278
1279
1280
1281
1282
1283
1284
1285
1286
1287
1288
1289
1290
1291
1292
1293
1294
1295
1296
1297
1298
1299
1300
1301
1302
1303
1304
1305
1306
1307
1308
1309
1310
1311
1312
1313
1314
1315
1316
1317
1318
1319
1320
1321
1322
1323
1324
1325
1326
1327
1328
1329
1330
1331
1332
1333
1334
1335
1336
1337
1338
1339
1340
1341
1342
1343
1344
1345
1346
1347
1348
1349
1350
1351
1352
1353
1354
1355
1356
1357
1358
1359
1360
1361
1362
1363
1364
1365
1366
1367
1368
1369
1370
1371
1372
1373
1374
1375
1376
1377
1378
1379
1380
1381
1382
1383
1384
1385
1386
1387
1388
1389
1390
1391
1392
1393
1394
1395
1396
1397
1398
1399
1400
1401
1402
1403
1404
1405
1406
1407
1408
1409
1410
1411
1412
1413
1414
1415
1416
1417
1418
1419
1420
1421
1422
1423
1424
1425
1426
1427
1428
1429
1430
1431
1432
1433
1434
1435
1436
1437
1438
1439
1440
1441
1442
1443
1444
1445
1446
1447
1448
1449
1450
1451
1452
1453
1454
1455
1456
1457
1458
1459
1460
1461
1462
1463
1464
1465
1466
1467
1468
1469
1470
1471
1472
1473
1474
1475
1476
1477
1478
1479
1480
1481
1482
1483
1484
1485
1486
1487
1488
1489
1490
1491
1492
1493
1494
1495
1496
1497
1498
1499
1500
1501
1502
1503
1504
1505
1506
1507
1508
1509
1510
1511
1512
1513
1514
1515
1516
1517
1518
1519
1520
1521
1522
1523
1524
1525
1526
1527
1528
1529
1530
1531
1532
1533
1534
1535
1536
1537
1538
1539
1540
1541
1542
1543
1544
1545
1546
1547
1548
1549
1550
1551
1552
1553
1554
1555
1556
1557
1558
1559
1560
1561
1562
1563
1564
1565
1566
1567
1568
1569
1570
1571
1572
1573
1574
1575
1576
1577
1578
1579
1580
1581
1582
1583
1584
1585
1586
1587
1588
1589
1590
1591
1592
1593
1594
1595
1596
1597
1598
1599
1600
1601
1602
1603
1604
1605
1606
1607
1608
1609
1610
1611
1612
1613
1614
1615
1616
1617
1618
1619
1620
1621
1622
1623
1624
1625
1626
1627
1628
1629
1630
1631
1632
1633
1634
1635
1636
1637
1638
1639
1640
1641
1642
1643
1644
1645
1646
1647
1648
1649
1650
1651
1652
1653
1654
1655
1656
1657
1658
1659
1660
1661
1662
1663
1664
1665
1666
1667
1668
1669
1670
1671
1672
1673
1674
1675
1676
1677
1678
1679
1680
1681
1682
1683
1684
1685
1686
1687
1688
1689
1690
1691
1692
1693
1694
1695
1696
1697
1698
1699
1700
1701
1702
1703
1704
1705
1706
1707
1708
1709
1710
1711
1712
1713
1714
1715
1716
1717
1718
1719
1720
1721
1722
1723
1724
1725
1726
1727
1728
1729
1730
1731
1732
1733
1734
1735
1736
1737
1738
1739
1740
1741
1742
1743
1744
1745
1746
1747
1748
1749
1750
1751
1752
1753
1754
1755
1756
1757
1758
1759
1760
1761
1762
1763
1764
1765
1766
1767
1768
1769
1770
1771
1772
1773
1774
1775
1776
1777
1778
1779
1780
1781
1782
1783
1784
1785
1786
1787
1788
1789
1790
1791
1792
1793
1794
1795
1796
1797
1798
1799
1800
1801
1802
1803
1804
1805
1806
1807
1808
1809
1810
1811
1812
1813
1814
1815
1816
1817
1818
1819
1820
1821
1822
1823
1824
1825
1826
1827
1828
1829
1830
1831
1832
1833
1834
1835
1836
1837
1838
1839
1840
1841
1842
1843
1844
1845
1846
1847
1848
1849
1850
1851
1852
1853
1854
1855
1856
1857
1858
1859
1860
1861
1862
1863
1864
1865
1866
1867
1868
1869
1870
1871
1872
1873
1874
1875
1876
1877
1878
1879
1880
1881
1882
1883
1884
1885
1886
1887
1888
1889
1890
1891
1892
1893
1894
1895
1896
1897
1898
1899
1900
1901
1902
1903
1904
1905
1906
1907
1908
1909
1910
1911
1912
1913
1914
1915
1916
1917
1918
1919
1920
1921
1922
1923
1924
1925
1926
1927
1928
1929
1930
1931
1932
1933
1934
1935
1936
1937
1938
1939
1940
1941
1942
1943
1944
1945
1946
1947
1948
1949
1950
1951
1952
1953
1954
1955
1956
1957
1958
1959
1960
1961
1962
1963
1964
1965
1966
1967
1968
1969
1970
1971
1972
1973
1974
1975
1976
1977
1978
1979
1980
1981
1982
1983
1984
1985
1986
1987
1988
1989
1990
1991
1992
1993
1994
1995
1996
1997
1998
1999
2000
2001
2002
2003
2004
2005
2006
2007
2008
2009
2010
2011
2012
2013
2014
2015
2016
2017
2018
2019
2020
2021
2022
2023
2024
2025
2026
2027
2028
2029
2030
2031
2032
2033
2034
2035
2036
2037
2038
2039
2040
2041
2042
2043
2044
2045
2046
2047
2048
2049
2050
2051
2052
2053
2054
2055
2056
2057
2058
2059
2060
2061
2062
2063
2064
2065
2066
2067
2068
2069
2070
2071
2072
2073
2074
2075
2076
2077
2078
2079
2080
2081
2082
2083
2084
2085
2086
2087
2088
2089
2090
2091
2092
2093
2094
2095
2096
2097
2098
2099
2100
2101
2102
2103
2104
2105
2106
2107
2108
2109
2110
2111
2112
2113
2114
2115
2116
2117
2118
2119
2120
2121
2122
2123
2124
2125
2126
2127
2128
2129
2130
2131
2132
2133
2134
2135
2136
2137
2138
2139
2140
2141
2142
2143
2144
2145
2146
2147
2148
2149
2150
2151
2152
2153
2154
2155
2156
2157
2158
2159
2160
2161
2162
2163
2164
2165
2166
2167
2168
2169
2170
2171
2172
2173
2174
2175
2176
2177
2178
2179
2180
2181
2182
2183
2184
2185
2186
2187
2188
2189
2190
2191
2192
2193
2194
2195
2196
2197
2198
2199
2200
2201
2202
2203
2204
2205
2206
2207
2208
22

入帳票編號: 06437754

Chit No.:

選擇「✓」一個訂明設施:

Tick (✓) One Prescribed Facility:

☐ 堆填區 ☐ 篩選分類設施
Landfills Sorting Facilities

☐ 公眾填料接收設施
Public Fill Reception Facilities

☐ 離島廢物轉運設施
Outlying Islands Transfer Facilities

車牌號碼 Vehicle Registration Mark:

使用日期:

Date of Use:

簽發人:

Issued by:

建築廢物產生地點:

 Construction Waste Generated Site:
STONECUTTERS ISLAND
SEWAGE TREATMENT PLANT

入帳票編號: 06437754

Chit No.:

選擇「✓」一個訂明設施:

Tick (✓) One Prescribed Facility:

☐ 堆填區 ☐ 篩選分類設施
Landfills Sorting Facilities

☐ 公眾填料接收設施
Public Fill Reception Facilities

☐ 離島廢物轉運設施
Outlying Islands Transfer Facilities

車牌號碼 Vehicle Registration Mark:

使用日期:

Date of Use:

簽發人:

Issued by:

帳戶名稱:

 Name of the Account-holder:
CHINA STATE CONST ENG
(H.K.) LTD & ATAL ENG LTD
TRADING AS CHINA STATE
- ATAL JOINT VENTURE

 香港法例第354章廢物處置條例
廢物處置(建築廢物處置收費)規例
Waste Disposal Ordinance (Chapter 354)
Waste Disposal (Charges for Disposal of Construction Waste) Regulation

載運入帳票

CHIT

車牌號碼:

Vehicle Registration Mark:



0 6 4 3 7 7 5 4

有效期至: Not Applicable

Valid Until:

建築廢物產生地點:

 Construction Waste Generated Site:
STONECUTTERS ISLAND SEWAGE TREATMENT
PLANT

帳戶名稱:

 Name of the Account-holder:
CHINA STATE CONST ENG (H.K.) LTD & ATAL
ENG LTD TRADING AS CHINA STATE - ATAL
JOINT VENTURE

帳戶編號: 7011408

Account No.:

 甲部份: 由帳戶戶主保留
Part A: retained by Account-holder

帳戶編號: 7011408

Account No.:

 乙部份: 由廢物運輸商保留
Part B: retained by Waste Hauler

 CEDD 土木工程發展署
Civil Engineering and
Development Department

 環境保護署
Environmental
Protection Department


7 0 1 1 4 0 8

 丙部份: 由政府保留
Part C: retained by Government

A SAMPLE OF "DAILY RECORD SUMMARY" TO RECORD DAILY DISPOSAL OF CONSTRUCTION & DEMOLITION (C&D) MATERIALS FROM THE SITE

- (1) Contract no. & title: _____
- (2) Date of disposal: _____
- (3) Designated disposal ground(s): (a) _____
 (b) _____
 (c) _____
 others _____

(4) Approved alternative disposal grounds: _____

DDF Serial no.	Vehicle registration no.	Departure time from site	Approx. vol (e.g. Full/Three Quarter/Half/One quarter)	C&D material type (e.g. inert or non-inert)	Actual disposal ground	Arrival time at disposal ground	Remarks

Part 1¹ Part 2²

Submitted by :

Signature :

Date :

Received by :

Post :

Date & Time :

[Name of Contractor's Designated
Person]

Submitted by :

Signature :

Date :

Received by :

Post :

Date & Time :

[Name of Contractor's Designated Person]

[Name and signature of the officer]

¹ Part 1 - The Contractor shall complete Part 1 and submit it to the Engineer's Representative by 1:00 pm of the following working day of the disposal trip.

² Part 2 - The Contractor shall complete Part 2 and submit it to the Engineer's Representative within 3 working days of the disposal trip.

THE GOVERNMENT OF THE HKSAR
Fill Bank at Tuen Mun Area 38
TRANSACTION RECORD
香港特別行政區政府屯門第38區填料庫交收記錄

入帳票編號: 06437674

Chit No.:

選擇「✓」一個訂明設施:

Tick (✓) One Prescribed Facility:

☒ 堆填區 ☐ 篩選分類設施

☐ Landfills ☐ Sorting Facilities

☒ 公眾填料接收設施

☐ Public Fill Reception Facilities

☐ 離島廢物轉運設施

☐ Outlying Islands Transfer Facilities

車牌號碼 Vehicle Registration Mark:

LW1064

使用日期:

Date of Use:

24/11/2010

簽發人:

Issued by:

[Signature]

帳戶名稱:

Name of the Account-holder

CHINA STATE CONST ENG

(H.K.) LTD & ATAL ENG LTD

TRADING AS CHINA STATE

- ATAL JOINT VENTURE

92 11 2010

帳戶編號:

Account No.:

7011408

乙部份: 由廢物運商保留

Part B: retained by Waste Handler

Date:

日期

2010-11-29

Vehicle No.:

車輛登記號碼

LW1064

Time in:

進入時間

11:25:08

Source of Material:

物料來源地

Shamshui

Contract No.:

工程合約編號

OC/2009/17

Weight in (tonne):

入載重量 (公噸)

21.93

Net vehicle load (tonne):

物料淨重量 (公噸)

9.38

Amount (HK\$):

總款 (港幣)

253.80

Chit No.:

記帳單編號

06437674

Remarks:

備註

Trans. Ref. No.:

備考號碼

100284280

Classifying Label:

車輛標識類別

Time out:

離開時間

11:31:25

Type of Material:

物料類別

Mixed rock and soil

DDF Serial No.:

運載記錄票編號

0002944001

Weight out (tonne):

出載重量 (公噸)

12.55

Charged load (tonne):

收費重量 (公噸)

9.40

Account No.:

帳戶編號

7011408

拒進原因一覽表

R1: 物料不符合要求

XXXXXXXXXX

R3: 無有效卸泥執照

XXXXXXXXXX

R4: 運載記錄票資料不符

XXXXXXXXXX

R5: 記帳戶已暫停/無效

XXXXXXXXXX

R6: VRM帳戶已暫停

XXXXXXXXXX

R7: 其它

XXXXXXXXXX

"This is not a formal record of payment. All information is subject to final verification."

此記錄並非正式收據。所有資料須經最後核實方可作實。

Serial No. 0002944001

Construction and Demolition Materials
Disposal Delivery Form
拆建物料運載記錄票

Serial No. 0002944001



Date: 29-11-2010
日期: 29-11-2010

Designated PFF/Landfill:
指定公眾填土設施/堆填區:

TM38

Vehicle Licence Plate Number
車牌號碼:

LW1064

Issued By:
簽發

KJ

Derek Lau

92:11V 62 101

(Information contained in this form may be displayed on Internet 此表格所載資料可被上載於互聯網)

Date: Time of departure from site

日期: 29-11-2010 離開地盤時間: 10:30

Vehicle Licence Plate Number:

車牌號碼: LW1064

Designated Public Filling Facility/Landfill:

指定公眾填土設施/堆填區:

TM38

Location of Site:

地盤位置:

- | | | | | |
|---|---|--|--|---|
| <input type="checkbox"/> Central & Western
中西區 | <input type="checkbox"/> Wanchai
灣仔 | <input type="checkbox"/> Eastern
東區 | <input type="checkbox"/> Southern
南區 | <input type="checkbox"/> Sai Kung
西貢 |
| <input type="checkbox"/> Yau, Tsim, Mong
油尖旺 | <input checked="" type="checkbox"/> Shamshuipo
深水埗 | <input type="checkbox"/> Kowloon City
九龍城 | <input type="checkbox"/> Wong Tai Sin
黃大仙 | <input type="checkbox"/> Outlying Islands
離島 |
| <input type="checkbox"/> Kwun Tong
觀塘 | <input type="checkbox"/> Kwai Tsing
葵青 | <input type="checkbox"/> Tsuen Wan
荃灣 | <input type="checkbox"/> Tuen Mun
屯門 | <input type="checkbox"/> Shatin
沙田 |
| <input type="checkbox"/> Yuen Long
元朗 | <input type="checkbox"/> North
北區 | <input type="checkbox"/> Tai Po
大埔 | | |

Approximate Load ☐ 1/4 ☐ 1/2 ☒ 3/4 ☐ Full滿
大約承載量:

Contract No. DC/2009/17



DC200917

Please stick contract no. barcode above
請在上方貼上合約編號條碼



Chop of Designated Public Filling Facility/
Landfill 公眾填土設施/堆填區蓋印

Chop of Designated Public Filling Facility/Landfill
公眾填土設施/堆填區蓋印

Chop of Engineer's/Architect's Representative
工程師/建築師代表蓋印
