#### MONTHLY EM&A REPORT

The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: 52<sup>nd</sup> Monthly EM&A Report (1 February to 29 February 2016)

Issue Date: March 2016

**Environmental Resources Management** 

16/F Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

#### MONTHLY EM&A REPORT

The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: 52<sup>nd</sup> Monthly EM&A Report (From 1 February to 29 February 2016)

Issue Date: March 2016

Reference 0095646

For and on	behalf of			
ERM-Hong	ERM-Hong Kong, Limited			
_	-			
Approved b	by: Frank Wan			
Signed:	handerth J.			
Position:	Partner			
Certified by				
	vironmental Team Leader – Katie Yu)			
Date: _	9 March 2016			

This report has been prepared by ERM-Hong Kong, Limited with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client.

We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.

This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.



**阿特金斯 ATKINS** 香港九龍尖沙咀海港城 九倉電訊中心十三樓 13/F Wharf T&T Centre Harbour City Tsim Sha Tsui Kowloon Hong Kong

Telephone (852) 2972 1000 Facsimile (852) 2890 6343

info.hk@atkinsglobal.com www.atkinsglobal.com

Your ref.	0095646_let_Atkins_20160310 Monthly EM&A Report No.52.doc
Our ref.	5121189/17.20/OC096/SO/EK

Date: 10 March 2016

#### By Post and Email (katie.yu@erm.com)

ERM-Hong Kong Limited, 16/F Berkshire House, 25 Westlands Road, Quarry Bay, Hong Kong

Attn: Ms Katie Yu

Dear Katie,

#### Central Police Station Conservation and Revitalization Project Verification of Monthly EM&A Report No. 52

We refer to your letter dated 10 March 2016 regarding the Monthly EM&A Report No. 52. Atkins China Limited verifies, in the capacity of Independent Environmental Checker, that the report conforms the requirements provided in Condition 3.4 of the Environmental Permit (EP-408/2011/B).

Yours sincerely, For Atkins China Limited

maifal

Sharifah Or Independent Environmental Checker

c.c. HKJC – Mr. Kenneth Lee (By Email) Rocco Design Architect – Mr. Charles Kung (By Email)

1	INTRODUCTION	1
1.1	PURPOSE OF THE REPORT	1
1.2	STRUCTURE OF THE REPORT	1
2	PROJECT INFORMATION	3
2.1	BACKGROUND	3
2.2	SITE DESCRIPTION	3
2.3	CONSTRUCTION ACTIVITIES	3
2.4	PROJECT ORGANISATION	4
2.5	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	4
3	ENVIRONMENTAL MONITORING REQUIREMENTS	8
3.1	NOISE MONITORING	8
3.1.1	Monitoring Location	8
3.1.2	Monitoring Parameters, Frequency and Programme	8
3.1.3	Monitoring Equipment and Methodology	8
3.1.4	Event / Action Plan	9
3.1.5	Mitigation Measures	9
3.2	Cultural Heritage	8
3.2.1	Vibration Monitoring	8
3.2.2	Mitigation Measures	9
3.3	LANDSCAPE AND VISUAL MONITORING	11
3.3.1	Mitigation Measures	11
3.4	Environmental Requirements in Contract Documents	11
4	IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS	12
5	MONITORING RESULTS	13
5.1	NOISE	13
5.2	CULTURAL HERITAGE	13
5.3	LANDSCAPE AND VISUAL	14
5.4	WASTE MANAGEMENT	15
6	ENVIRONMENTAL SITE INSPECTION	16
7	ENVIRONMENTAL NON-CONFORMANCE	17
7.1	SUMMARY OF MONITORING EXCEEDANCE	17
7.2	SUMMARY OF ENQUIRY	17
7.3	SUMMARY OF ENVIRONMENTAL NON-COMPLIANCE	17
7.4	SUMMARY OF ENVIRONMENTAL COMPLAINT	17
7.5	SUMMARY OF ENVIRONMENTAL SUMMONS AND SUCCESSFUL PROSECUTION	17

#### 8 FUTURE KEY ISSUES

8.1	Key Issues for the Coming Month	18
8.2	MONITORING SCHEDULE FOR THE NEXT MONTH	10
8.3	CONSTRUCTION PROGRAMME FOR THE NEXT MONTH	18
0.0		10
9	CONCLUSIONS	19

18

#### LIST OF TABLES

Table 2.1	Summary of Construction Activities Undertaken from 1 to 29
	February 2016

- Table 2.2
   Summary of Environmental Licensing, Notification and Permit Status
- Table 3.1
   Construction Phase Noise Monitoring Station
- Table 3.2
   Noise Monitoring Equipment
- Table 3.3 Action and Limit Levels for Construction Noise Monitoring
- Table 3.4 Alert, Alarm and Action (AAA) Levels for Vibration Monitoring
- Table 3.5 Event and Action Plan for Vibration Monitoring
- Table 4.1
   Status of Required Submissions
- Table 5.1 Findings of Monthly Tree Inspection in the Reporting Period
- Table 5.2 Quantities of Waste Generated from the Project
- Table 8.1
   Construction Works to be Undertaken in the Coming One Month

#### LIST OF ANNEXES

Annex A	Locations of Works Areas and the Surroundings
Annex A1	Project Location
Annex A2	Declared Monuments within the Project Site
Annex A3	Site Layout Plan marked with Works
Annex B	Project Organization Chart and Contact Detail
Annex C	Locations of Noise Monitoring Stations and Noise Sensitive Receivers
Annex D	Monitoring Schedule of the Reporting Month and the Next Month
Annex E	Calibration Reports for Calibrators and Sound Level Meters
Annex F	Event /Action Plans for Noise
Annex G	Summary of Implementation Status
Annex H	Noise Monitoring Results
Annex I	Construction Programme for the Project

Annex J	Tree Inspection Reports
Annex K	Environmental Complaint, Environmental Summons and Prosecution Log
Annex L	Records of Vibration Monitoring for Trial Piling and Pipe / Bored Piling Works
Annex M	Records of Vibration Monitoring for Other Construction Works

#### **EXECUTIVE SUMMARY**

The construction works of **Central Police Station Conservation and Revitalisation Project** commenced on 24 October 2011. This is the 52<sup>nd</sup> monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the period from 1 to 29 February 2016 in accordance with the EM&A Manual.

#### Summary of Construction Works undertaken during Reporting Period

The major construction works undertaken during the reporting period include:

- Structural addition and alteration works at Blocks 4 and 14;
- Roof repair works at Block 4;
- Balcony repair at Blocks 6 and 7;
- Plaster repair at Blocks 3 and 14;
- Timber doors and windows repair works at Blocks 3 and 9;
- Structural timber floor repair at Blocks 4;
- Metal works repair at Block 14;
- Façade works at Blocks 14 and 17;
- Arbuthnot Wing & Old Bailey Wing fitout works;
- Old Bailey Wing external facade installation;
- E&M Opening at Blocks 9 and 14;
- E&M installation at Blocks 3, 9, 14, Arbuthnot Wing and Old Bailey Wing;
- U/G Drainage sitewide (M1, M6A, U3); and
- Footbridge construction.

#### Environmental Monitoring and Audit Progress

A summary of the monitoring activities in this reporting period is listed below:

٠	<ul> <li>Construction noise monitoring during normal weekdays at each</li> </ul>		
	monitoring station	6 times	
٠	Joint environmental site inspection	1 time	
٠	Heritage site inspections	14 times	
٠	Landscape & visual monitoring	1 time	
٠	Tree inspection	1 time	
٠	Vibration monitoring for piling works	22 times	
٠	Vibration monitoring for other construction works	22 times	

#### <u>Noise</u>

6 sets of 30-minute construction noise measurements were carried out at each of the monitoring stations (NM2 and NM6) during normal weekdays of the

reporting period. No exceedance of the Action or Limit Level of construction noise was recorded during the reporting period.

#### <u>Cultural Heritage</u>

Vibration monitoring carried out for the trial piling and piling works during the reporting period are listed below:

• 22 vibration monitoring measurements at Block 8;

Vibration monitoring carried out for other construction works during the reporting period are listed below:

• 22 vibration monitoring measurements for the structural addition and alteration works at Block 11.

No exceedance of the Alert, Alarm and Action Levels was recorded during the reporting period.

Heritage site audits were conducted on 2-5, 11-12, 17-19, 22-26 February 2016 by the Heritage Checker during the reporting period. Major observations and recommendations during the site inspections were listed below:

#### 2 February 2016

• Inappropriate pipework and fixing were observed at Block 3 verandah. The Contractor was informed to follow up.

#### 5 February 2016

• It was observed that eight hose reels were installed on incorrect levels at Block 3 verandah. The Contractor was informed to follow up.

#### 24 February 2016

- It was observed that the existing paint on metal bars and mesh on the window at Block 9 holding cell were removed incorrectly. The Contractor was informed to follow up.
- Defects on doors at Block 11 were observed. The Contractor was informed to follow up.
- The original timber floorboards at Bock 19 were found missing. The Contractor was informed to follow up.

#### 26 February 2016

• It was observed that the structural repairs to brickwork has not commenced prior to E&M installation in Room 14/G/33 at Block 14. The Contractor was informed to follow up.

The Contractor was urged to follow-up the necessary rectification based on the inspection findings.

The follow-up actions recommended in the heritage site audits from the last reporting period (January 2016) have generally been implemented.

#### Landscape & Visual

Landscape and visual monitoring has commenced since October 2011 on a monthly basis. Tree inspection was conducted on 3 February 2016 by the arborist during the reporting period. Signs of pest (mealy bugs) at Tree-5 have been reduced due to pest control. The Contractor was recommended to keep monitoring of the pest for Tree-5. Withered leaves observed at Tree-11 in the previous inspections have reduced. The Contractor was reminded to keep close monitoring on the growth of the trees. Construction materials observed near the planter of Tree-11 in the previous inspections have been removed and the planter area is kept clear.

#### Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. A total of 274.16 tonnes of inert C&D materials were generated during the reporting period. 128.66 tonnes of non-inert C&D materials comprising general refuse were generated and disposed of at the SENT Landfill. 170 kg of paper/cardboard packaging was generated and recycled during the reporting period. No metal or plastic waste was recycled during the reporting period. No chemical waste was produced during the reporting.

#### Environmental Site Inspection

A joint environmental site inspection was carried out by the representatives of the Contractor, the IEC and the ET on 18 February 2016. A chemical waste container without chemical label was observed near Block 17. The Contractor was reminded to provide chemical label and move the chemical waste container to the chemical waste store.

# Environmental Exceedance/Non-conformance/Compliant/Summons and Prosecution

No exceedance of the Action or Limit Level of construction noise was recorded at designated monitoring stations during the reporting period.

No exceedance of the Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

No enquiry was received during the reporting period.

No non-compliance event was recorded during the reporting period.

No complaint was received during the reporting period.

No summons/prosecution was received during the reporting period.

#### Future Key Issues

Works to be undertaken in the next month include:

- Structural addition and alteration works at Blocks 4;
- Balcony repair at Blocks 6;
- Plaster repair at Blocks 3 and 14;
- Timber doors and windows repair works at Blocks 3;
- Structural timber floor repair at Block 4;
- Metal works repair at Block 14;
- Façade works at Blocks 14 and 17;
- Fitout works at Arbuthnot Wing and Old Bailey Wing;
- External façade installation at Old Bailey Wing;
- E&M installation at Blocks 3, 9, 14, Arbuthnot Wing and Old Bailey Wing;
- Underground drainage sitewide (M1, U3);
- Footbridge construction;
- Barracks lane stair construction and
- FSD inspection.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoff and waste management.

#### 1 INTRODUCTION

ERM-Hong Kong, Limited (ERM) was appointed by the Jockey Club CPS Limited (the CPS Ltd) as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the **Central Police Station Conservation and Revitalisation Project** (the Project).

#### 1.1 PURPOSE OF THE REPORT

This is the 52<sup>nd</sup> EM&A report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from **1** to **29 February 2016**.

#### **1.2** STRUCTURE OF THE REPORT

The structure of the report is as follows:

#### Section 1: Introduction

details the scope and structure of the report.

#### Section 2: Project Information

summarises background and scope of the Project, site description, project organization and contact details, construction programme, the construction works undertaken and the status of Environmental Permit(s)/License(s) during the reporting period.

#### Section 3: Environmental Monitoring Requirements

summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event/Action Plans, environmental mitigation measures as recommended in the EIA report and relevant environmental requirements.

### Section 4 : Implementation Status on Environmental Protection Requirements

summarises the implementation of environmental protection measures during the reporting period.

## Section 5 : Monitoring Results

summarises the monitoring results obtained in the reporting period.

#### Section 6: **Environmental Site Inspection** summarises the audit findings of the site inspections undertaken within the reporting period.

#### Section 7: Environmental Non-conformance

summarises any monitoring exceedance, environmental complaints and environmental summons within the reporting period.

## Section 8: Future Key Issues

summarises the impact forecast and monitoring schedule for the next reporting month.

Section 9: Conclusions

#### 2.1 BACKGROUND

The Chief Executive (CE)'s 2007-2008 Policy Address highlighted revitalisation as the guiding principle of heritage conservation and the Project was one of the specific proposals put forward by the CE in the same Policy Address. At the meeting of the Executive Council (ExCo) on 15 July 2008, the ExCo advised and the CE ordered that Government should enter into a partnership with the Hong Kong Jockey Club (HKJC) in the form of an agreement (or agreements) to take forward the conservation and revitalisation of the CPS project based on various guiding parameters. The Project is now being undertaken in partnership with the Development Bureau of the HKSAR Government. The HKJC has taken on board the decision at the ExCo meeting and further investigated the design and implementation of the Project. The Project is now implemented by the Jockey Club CPS Limited.

#### 2.2 SITE DESCRIPTION

The location of the Project Site is shown in *Annex A1*. The Site is bounded by Hollywood Road to the north, Arbuthnot Road to the east, Chancery Lane to the south and Old Bailey Street to the west.

The Site comprises three Declared Monuments designated under the *Antiquities and Monuments Ordinance* in 1995. They are:

- Central Police Station;
- Former Central Magistracy; and
- Victoria Prison Compound.

They are collectively named the Central Police Station (CPS). *Annex A2* shows the location of the Declared Monuments within CPS and the buildings within the CPS.

#### 2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in this reporting period is shown in *Table 2.1* and illustrated in *Annex A3*.

#### **Construction Activities Undertaken**

- Structural addition and alteration works at Blocks 4 and 14;
- Roof repair works at Block 4;
- Balcony repair at Blocks 6 and 7;
- Plaster repair at Blocks 3 and 14;
- Timber doors and windows repair works at Blocks 3 and 9;
- Structural timber floor repair at Blocks 4;
- Metal works repair at Block 14;
- Façade works at Blocks 14 and 17;
- Arbuthnot Wing & Old Bailey Wing fitout works;
- Old Bailey Wing external facade installation;
- E&M Opening at Blocks 9 and 14;
- E&M installation at Blocks 3, 9, 14, Arbuthnot Wing and Old Bailey Wing;
- U/G Drainage sitewide (M1, M6A, U3); and
- Footbridge construction.

#### 2.4 **PROJECT ORGANISATION**

The Project organisation chart and contact details are shown in *Annex B*.

#### 2.5 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the relevant permits, licences, and/or notifications on environmental protection for this Project since the granting of the EP in April 2011 is presented in *Table 2.2*.

Permit/ Licences/ Notification	Reference	Validity Period	Remarks	
Environmental Permit (EP)	EP-408/2011 -		Superseded on 10 January 2012	
	EP-408/2011/A	-	Superseded on 22 March 2012	
	EP-408/2011/B	Throughout the Contract	Permit granted on 22 March 2012	
Notification of Construction Works as required under <i>Air</i> <i>Pollution Control</i> (Construction Dust) Regulation	Ref. No. 332920	Throughout the Contract	-	
Registration of Chemical Waste Producer under Waste Disposal Ordinance	Chemical Waste Producer No.: 5213- 122-G2347-25	Throughout the Contract	-	
Disposal of C&D material/waste	Billing Account Number: 7013338	Throughout the Contract	-	
Effluent Discharge License under Water Pollution Control Ordinance	License No. WT00010633-2011	21 Oct 2011 – 31 Oct 2016	-	
Notification of Commencement of Asbestos Abatement Work under <i>Air</i> <i>Pollution Control</i> <i>Ordinance</i>	-	Throughout the Contract	EPD's letter (EPD's ref.: (5) in EPAC/A/4/000/23 3 II) dated 2 December 2011 satisfied that the content of the asbestos abatement plan (Report No.: 0210/11/ED/0078A ) is in accordance with the APCO	
Approval of Asbestos Abatement Work (Phase 2)	-	Earliest commencement date on 26 January 2012	EPD's letter (EPD's ref:() in EPAC/A/4/000/23 3) dated 18 January 2012.	
Construction Noise Permit (CNP)	GW-RS0734-12	11 July 2012 at 0200 hours to 2 August 2012 at 0400 hours	Expired.	
	GW-RS0839-12	13 August 2012 at 1900 hours to 31 December 2012 at 0700 hours	Expired.	
	GW-RS1162-12	1 December 2012 at 0000 hours to 28 March 2013 at 0600 hours	Expired.	
	GW-RS0113-13	1 February 2013 at 0200 hours to 31	Expired.	

ENVIRONMENTAL RESOURCES MANAGEMENT

THE JOCKEY CLUB CPS LIMITED

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
		May 2013 at 0400 hours	
	GW-RS1301-12	2 January 2013 at 1900 hours to 29 June 2013 at 2300 hours	Expired.
	GW-RS0084-13	24 January 2013 at 1900 hours to 29 June 2013 at 0700 hours	Expired.
	GW-RS0638-13	16 June 2013 at 0700 hours to 15 September 2013 at 1900 hours	Expired.
	GW-RS0901-13	14 August 2013 at 0000 hours to 31 October 2013 at 0600 hours	Expired.
	GW-RS0714-13	29 June 2013 at 1900 hours to 28 December 2013 at 2400 hours	Expired.
	GW-RS0745-13	5 July 2013 at 1900 hours to 30 December 2013 at 2300 hours	Expired.
	GW-RS1110-13	7 October 2013 at 0200 hours to 31 December 2013 at 0400 hours	Expired.
	GW-RS1205-13	4 November 2013 at 0000 hours to 30 January 2014 at 2400 hours	Expired.
	GW-RS1275-13	13 November 2013 at 0000 hours to 30 April 2014 at 2400 hours	Expired.
	GW-RS0062-14	10 February 2014 at 0000 hours to 31 March 2014 at 2400 hours.	Expired.
	GW-RS1461-13	29 December 2013 at 0000 hours to 28 June 2014 at 2400 hours.	Expired.
	GW-RS0271-14	1 April 2014 at 0100 hours to 30 June 2014 at 0600 hours	Expired.
	GW-RS0434-14	8 May 2014 at 0000 hours to 30 September 2014 at 2400 hours	Expired.
	GW-RS0651-14	28 July 2014 at 0000	Expired.

THE JOCKEY CLUB CPS LIMITED

Permit/ Licences/ Notification	Reference	Validity Period	Remarks	
		hours to 26 September 2014 at 2400 hours		
	GW-RS0658-14	29 June 2014 at 0000 hours to 28 December 2014 at 2400 hours	Expired.	
	GW-RS0918-14	29 September 2014 at 0000 hours to 31 December 2014 at 2400 hours	Expired.	
	GW-RS0749-14	1 August 2014 at 0000 hours to 31 January 2015 at 2400 hours	Expired.	
	GW-RS0044-15	16 March 2015 at 0100 hours to 24 April 2015 at 0500 hours	Expired.	
	GW-RS0086-15	1 February 2015 at 0000 hours to 30 June 2015 at 2400 hours	Expired.	
	GW-RS0280-15	27 April 2015 at 0000 hours to 26 May 2015 at 2400 hours	Expired.	
	GW-RS0693-15	6 July 2015 at 0000 hours to 30 July 2015 at 2400 hours	Expired.	
	GW-RS0707-15	1 July 2015 at 0000 hours to 29 December 2015 at 2400 hours	Cancelled by EPD on 31 July 2015.	
	GW-RS0241-15	23 March 2015 at 0000 hours to 21 August 2015 at 2400 hours	Expired.	
	GW-RS0580-15	28 May 2015 at 0000 hours to 25 August 2015 at 2400 hours	Expired.	
	GW-RS0514-15	21 May 2015 at 0000 hours to 20 November 2015 at 2400 hours	Expired.	
	GW-RS0696-15	28 June 2015 at 0000 hours to 29 November 2015 at 2400 hours	Expired.	
	GW-RS1301-15	30 November 2015 at 0000 hours to 29 May 2016 at 2400 hours	-	

#### 3.1 NOISE MONITORING

#### 3.1.1 Monitoring Location

The construction noise monitoring locations are listed in *Table 3.1* and are shown in *Annex C*.

#### Table 3.1Construction Phase Noise Monitoring Station

Monitoring Location	Proposed Construction Noise Monitoring Station			
	ID in EM&A Manual	ID	Type of Measurement	Remark
Rooftop of Ho Fook Building	N2	NM2	Façade	-
Rooftop of Chancery Mansion		NM6	Façade	Accesses to the original proposed monitoring location in the EM&A Manual, Chancery House (N5), were denied; alternative location of Chancery Mansion (N6), were therefore proposed and approved by the Authorised Person (AP), the Independent Environmental Checker (IEC) and EPD.

The noise sensitive receivers are also shown in Annex C.

#### 3.1.2 Monitoring Parameters, Frequency and Programme

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. The monitoring programme for this reporting period is shown in *Annex D*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ) in decibels dB(A).  $L_{eq (30min)}$  were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays. Supplementary information for data auditing, two statistical sound levels  $L_{10}$  and  $L_{90}$  - the levels exceeded for 10 and 90 percent of the time respectively, were also recorded during the monitoring for reference. The measured noise levels were logged in every 5 minutes throughout the impact monitoring period.

#### 3.1.3 Monitoring Equipment and Methodology

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures* of *Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO)* (Cap 400).

The sound level meters and calibrator used for the noise measurement, as listed in *Table 3.2*, complies with the IEC 651: 1979 and 804:1985 (Type 1) specifications. The calibration certificates of the sound level meters are appended in *Annex E*.

#### Table 3.2Noise Monitoring Equipment

Monitoring Stations	Monitoring Equipment (Sound Level Meter and Calibrator)
NM2, NM6	<u>Calibrator</u> CEL 120 (S/N 3421612)
	Sound Level Meter
	CEL-633A (S/N 3521757)

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

Measurements were accepted as the calibration level from before and after the noise measurement agree to within 1.0 dB(A).

#### 3.1.4 Event / Action Plan

#### Table 3.3 Action and Limit Levels for Construction Noise Monitoring

Noise Monitoring Location	Action Level	Limit Level, L <sub>eq(30mins), dB(A)</sub>	Remark
NM2, NM6	When one documented complaint is received from any one of the sensitive receivers	75 (note)	Applicable during 0700 – 1900 hours on normal weekdays.
Notes:			
70dB(A) for sc (b) If works are to	hools and 65dB(A) dur	ing school examina restricted hours, the	./B/C. Limit Level is reduced to tion periods. e conditions stipulated in the CNP

The Event / Action Plan (EAP) for noise monitoring is presented in Annex F.

#### 3.1.5 *Mitigation Measures*

The mitigation measures in accordance with the EP, EIA and EM&A Manual and their implementation status are presented in *Annex G*.

#### 3.2 CULTURAL HERITAGE

#### 3.2.1 Vibration Monitoring

In accordance with the EM&A Manual, vibration monitoring is required and the vibration control limits and vibration monitoring proposal are defined by a specialist for AMO's approval.

#### **Baseline Monitoring**

A set of initial readings should be recorded prior to commencement of each stage of demolition works or trial piling works. The baseline vibration monitoring should be conducted for duration of 5 minutes on the measurement day(s) at each vibration monitoring location.

#### Vibration Monitoring for Demolition Works

There are five phases/stages of vibration monitoring to be carried out for demolition works, namely Initial Reading Phase, Monitoring Stage 1, Monitoring Stage 2, Monitoring Stage 3 and Monitoring Stage 4. The vibration monitoring should be conducted for duration of 5 minutes on the days with demolition works at each vibration monitoring location.

#### Vibration Monitoring for Trial Piling and Pipe/Bored Piling Works

Vibration monitoring for trial piling works and pipe/bored piling works is required. The monitoring location is shown in *Annex L*. The vibration monitoring should be conducted for duration of 5 minutes on the days with trial piling works or pipe/bored piling works at each vibration monitoring location.

#### Vibration Monitoring for Other Construction Works

Vibration monitoring for specific construction works other than demolition works, trial piling works and pipe/bored piling works is also required in accordance with Building Department's requirement. The monitoring location is shown in *Annex M*. The number and location of monitoring location will depend on the location of the specific construction works. The vibration monitoring should be conducted for duration of 5 minutes on a daily basis (working day) at each vibration monitoring location.

#### Alert, Alarm and Action Levels

The Alert, Alarm and Action (AAA) Levels are to be implemented during the vibration monitoring and shown in *Table 3.4*.

#### Table 3.4Alert, Alarm and Action (AAA) Levels for Vibration Monitoring

Instrument Type	Item Monitored	Alert Level	Alarm Level	Action Level
Vibration	Horizontal	2.0 mm/s	2.5 mm/s	3.0 mm/s
Monitoring	Movement			

The Event / Action Plan (EAP) for vibration monitoring is shown in Table 3.5.

Events	Action
Exceedance of Alert Level	Notify Management Contractor
Exceedance of Alarm Level	Notify Authorised Person/ Resident Engineer
Exceedance of Action Level	Cease Works and submit mitigation

#### 3.2.2 *Mitigation Measures*

Cultural heritage mitigation measures (including those for archaeology) in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

#### 3.3 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, inspections of affected trees were conducted by an experienced and appropriately trained arborist. All irregularities that deviate from the recommended tree protection measures or could impose deleterious impacts on the protected trees were reported. Besides, implementation of mitigation measures for landscape and visual resources recommended in the EIA Report were also monitored during the site inspection.

#### 3.3.1 Mitigation Measures

Landscape and visual mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

#### 3.4 Environmental Requirements in Contract Documents

The environmental requirements as specified in the contract documents were reviewed and were covered in the EIA's requirements.

#### IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS

The Contractor has generally implemented the environmental mitigation measures (including those for archaeology) and requirements as stated in the EIA Report, the EP and EM&A Manual and the contract documents. The implementation status during the reporting period is summarized in *Annex G*.

Status of required submissions under the EP during the reporting period is presented in *Table 4.1*.

#### Table 4.1Status of Required Submissions

4

Submission		Submission Date
EP Condition		
Condition 3.4	51st Monthly EM&A Report	12 February 2016

#### 5.1 NOISE

A total of 6 sets of 30-minute construction noise measurements were carried out at the monitoring stations (NM2 and NM6) during normal weekdays of the reporting period. The monitoring results together with graphical presentations are presented in *Annex H*. The local impacts observed near the monitoring stations of NM2 and NM6 were summarised below:

- NM2: construction noise from activities in the Project Site and traffic noise from Old Bailey Street.
- NM6: construction noise from activities in the Project Site and traffic noise from Chancery Lane.

No exceedance of the Action or Limit Level of construction noise was recorded during the reporting period.

#### 5.2 CULTURAL HERITAGE

#### 5.2.1 Vibration Monitoring

#### Trial Piling and Piling works

Vibration monitoring carried out for the trial piling and piling works during the reporting period are listed below:

• 22 vibration monitoring measurements at Block 8;

The monitoring results are presented in *Annex L*.

#### Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

• 22 vibration monitoring measurements for the structural addition and alteration works at Block 11.

The monitoring results are presented in Annex M.

All monitoring results were below the Alert/Alarm/Action Levels.

#### 5.2.2 Heritage Site Audit

Heritage site audits were conducted on 2-5, 11-12, 17-19, 22-26 February 2016 by the Heritage Checker during the reporting period. The cultural heritage requirements (including the recommended mitigation measures) stated in the approved EIA Report (AEIAR-162/2011) are being carried out. Major observations with respect to the requirements of the contract documents during the site inspections were listed below:

#### 2 February 2016

• Inappropriate pipework and fixing were observed at Block 3 verandah. The Contractor was informed to follow up.

#### 5 February 2016

• It was observed that eight hose reels were installed on incorrect levels at Block 3 verandah. The Contractor was informed to follow up.

#### 24 February 2016

- It was observed that the existing paint on metal bars and mesh on the window at Block 9 holding cell were removed incorrectly. The Contractor was informed to follow up.
- Defects on doors at Block 11 were observed. The Contractor was informed to follow up.
- The original timber floorboards at Bock 19 were found missing. The Contractor was informed to follow up.

#### 26 February 2016

• It was observed that the structural repairs to brickwork has not commenced prior to E&M installation in Room 14/G/33 at Block 14. The Contractor was informed to follow up.

The follow-up actions recommended in the heritage site audits from the last reporting period (January 2016) have generally been implemented.

#### 5.3 LANDSCAPE AND VISUAL

The tree inspection was conducted by the arborist on 3 February 2016 and major observations and recommendations in the reporting period are summarised in *Table 5.1*. The tree inspection report is contained in *Annex J*.

#### Table 5.1Findings of Monthly Tree Inspection in the Reporting Period

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observations / Recommendations
Tree -5	Mangifera indica	Fair	• To keep close monitoring on the presence of pest on the tree;
			• The planter is being re-built.
Tree -6	Aleurites moluccana	Fair	• No further action required.
Tree-7	Aleurites moluccana	Fair	• No further action required.
Tree-8	Plumeria rubra	Fair	• No further action required.

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observations / Recommendations
Tree-9	Araucaria cunninghamia	Fair	• No further action required.
Tree-11	Dracaena marginata	Fair	• Withered leaves on the lower braches have apparently reduced;
			<ul> <li>Construction materials observed near the planter in the previous inspections have been removed and the planter area is kept clear;</li> </ul>
			• To keep close monitoring on the growth of the tree;

#### 5.4 WASTE MANAGEMENT

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. Non-inert C&D materials were made up of wastes such as general refuse. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in Table 5.2. The non-inert C&D materials and general refuse generated from the Project were disposed of at the SENT Landfill. The inert C&D materials generated from the Project were disposed of at Chai Wan Public Fill Barging Point and Fill Bank at Tseung Kwan O Area 137. 170 kg of paper/cardboard packaging was generated and recycled during the reporting period. No metal or plastic waste was recycled during the reporting period. No chemical waste was produced during the reporting period.

#### Table 5.2 Quantities of Waste Generated from the Project

Month / Year			Qı	uantity			
_	C&D	C&D	Chemi	cal Waste	Recyc	led mater	ials
	Materials (inert) <sup>(a)</sup>	Materials (non-inert) <sup>(b)</sup>	Solid	Liquid	Paper / cardboard	Plastics	Metals
February	274.16	128.66	0 kg	0 L	170 kg	0 kg	0 kg
2016	tonnes	tonnes	-		-	-	-

Notes:

(a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil.

(b) The figure presented under non-inert C&D materials represents quantities of nonrecyclable materials such as general refuse which were disposed of at SENT Landfill. Recycled materials are reported separately.

Joint environmental site inspection was conducted by the representatives of the Contractor, IEC and the ET in the reporting period on 18 February 2016. There was no non-compliance recorded during the site inspection. Observations and recommendations were provided to the Contractor during the site inspection.

#### Follow-up Actions for the Last Site Audit

• Litter and construction materials observed at the planter of Tree-11 have been removed.

#### Observations and Recommendations of this Reporting Month

• A chemical waste container without chemical label was observed near Block 17. The Contractor was reminded to provide chemical label and move the chemical waste container to the chemical waste store.

#### 7 ENVIRONMENTAL NON-CONFORMANCE

#### 7.1 SUMMARY OF MONITORING EXCEEDANCE

No exceedance of the Action or Limit Level of construction noise or Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

#### 7.2 SUMMARY OF ENQUIRY

No enquiry was recorded during the reporting period.

#### 7.3 SUMMARY OF ENVIRONMENTAL NON-COMPLIANCE

No non-compliance event was recorded during the reporting period.

#### 7.4 SUMMARY OF ENVIRONMENTAL COMPLAINT

No complaint was received during the reporting period. The cumulative number of complaints is presented in *Annex K*.

7.5 SUMMARY OF ENVIRONMENTAL SUMMONS AND SUCCESSFUL PROSECUTION

No summons/prosecution was received during the reporting period.

#### 8.1 KEY ISSUES FOR THE COMING MONTH

Works to be undertaken for the coming monitoring period are summarised in *Table 8.1.* 

#### Table 8.1 Construction Works to be Undertaken in the Coming Month

#### Work to be Undertaken

- Structural addition and alteration works at Blocks 4;
- Balcony repair at Blocks 6;
- Plaster repair at Blocks 3 and 14;
- Timber doors and windows repair works at Blocks 3;
- Structural timber floor repair at Block 4;
- Metal works repair at Block 14;
- Façade works at Blocks 14 and 17;
- Fitout works at Arbuthnot Wing and Old Bailey Wing;
- External façade installation at Old Bailey Wing;
- E&M installation at Blocks 3, 9, 14, Arbuthnot Wing and Old Bailey Wing;
- Underground drainage sitewide (M1, U3);
- Footbridge construction;
- Barracks lane stair construction and
- FSD inspection.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoff and waste management.

#### 8.2 MONITORING SCHEDULE FOR THE NEXT MONTH

The tentative schedule of noise monitoring for the next reporting period is presented in *Annex D*.

#### 8.3 CONSTRUCTION PROGRAMME FOR THE NEXT MONTH

The most updated construction programme for the Project is presented in *Annex I*.

#### 9 CONCLUSIONS

The *Environmental Monitoring and Audit (EM&A) Report* presents the EM&A works undertaken during the period from 1 to 29 February 2016 in accordance with EM&A Manual and the requirement under EP-408/2011/B.

No exceedance of the Action or Limit Level of construction noise was recorded at designated monitoring stations during the reporting period.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

No enquiry was received during the reporting period.


No non-compliance event was recorded during the reporting period.


No complaint was received during the reporting period.

No summons/prosecution was received during the reporting period.

The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures. Annex A

Locations of Works Areas and the Surroundings

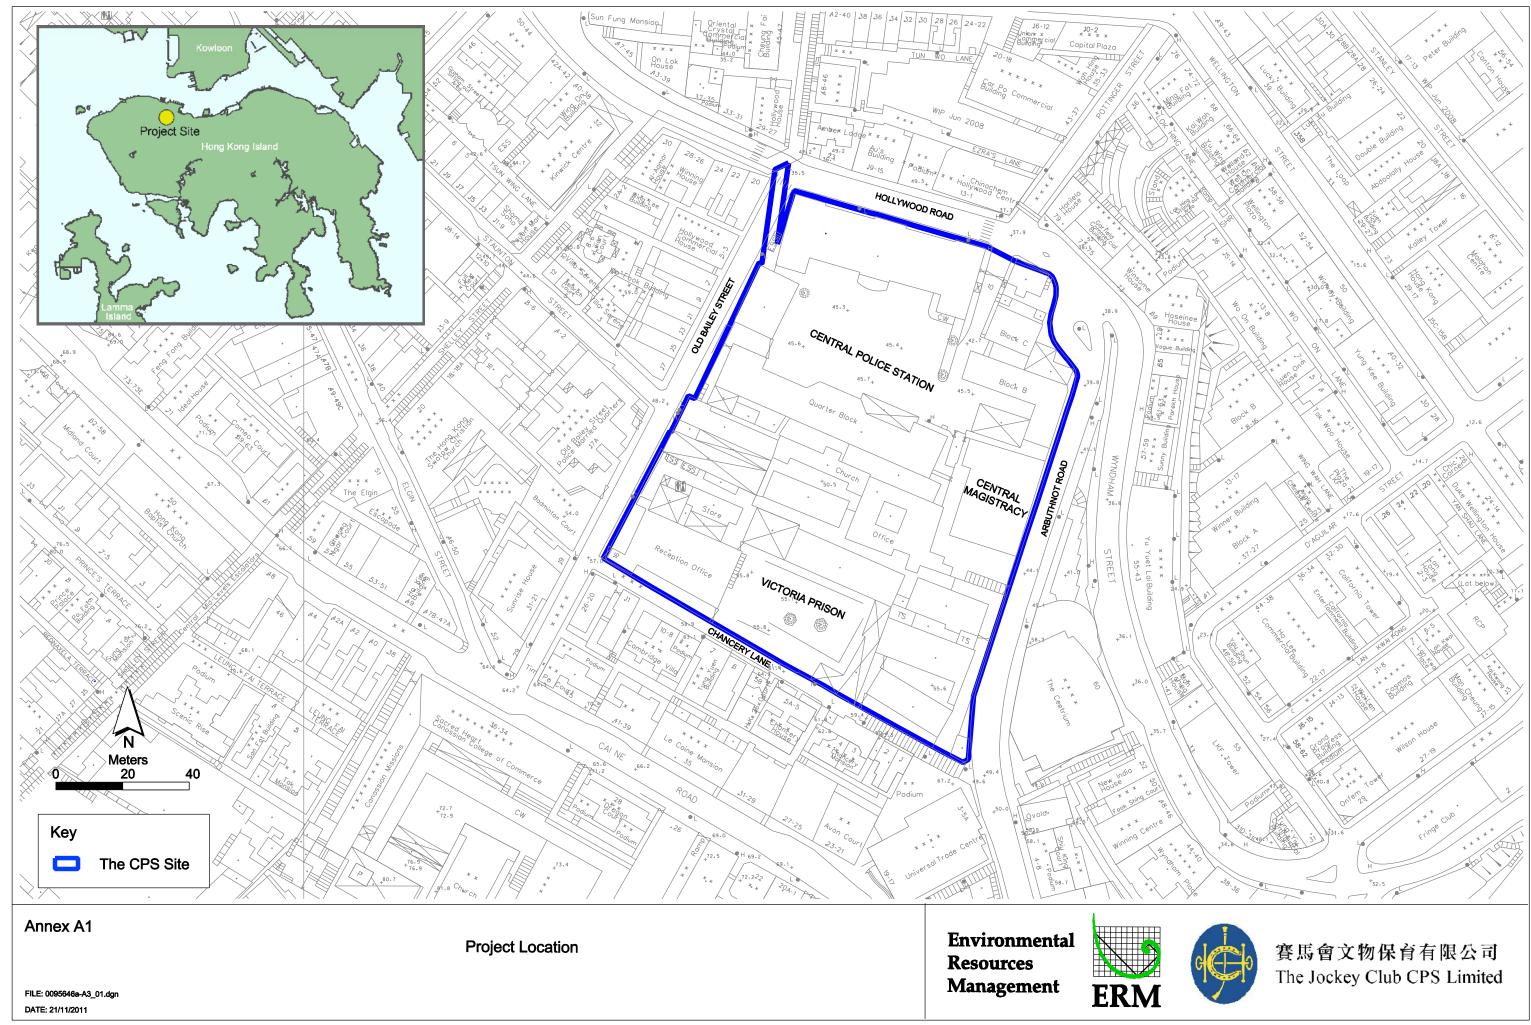

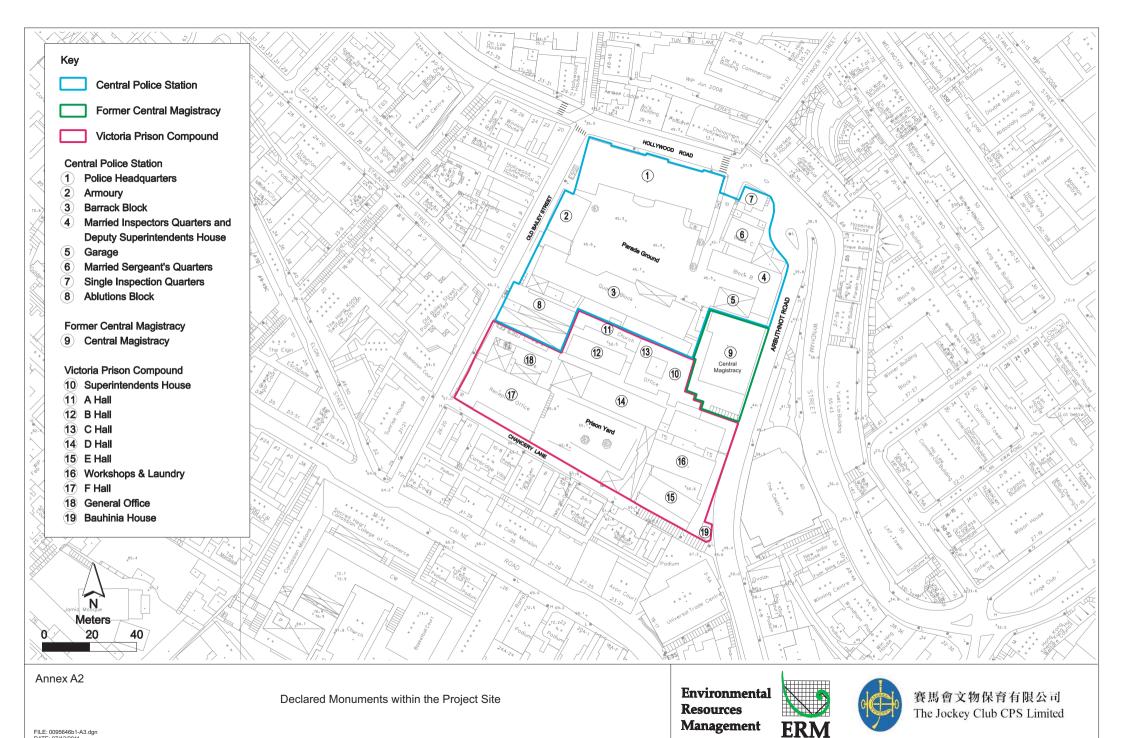

FILE: 0095646b1-A3.dgn DATE: 07/12/2011






۱.	E&M Installation / Opening / Conduit
	Transformer delivery and installation

- 2. Excavation
- 3. Internal Building Works
- 4. Permanent Steel Works Erection
- 5. Upgrading
- 6. Roof Replacement Works / New Roof / Repair
- 7. Basement Construction
- 8. Structure A&A Works
- 9. Repair Works to Timber Window, Door, Structure, Floor and Metal Elements
- **10. Demolition Works**
- 11. Facade Works / Link Bridage Repair
- **12. New Structure Construction**
- 13. Balcony Repair
- 14. Paint Stripping and Plastering Works
- 15. Core Wall Construction
- 16. Utilities Diversion and Carriageway
- 17. PBR
- 18. Removal of Needle Beams
- 19. U/G Drainage
- 20. Service trench construction
- 21. Demolition of concrete block
- 22. New Balcony Construction
- 23. Construction of terminal Manhole

Contractor	Gammon
Drawing Title	
· · · ·	
SITE LA'	YOUT PLAN
	Scole N.T.S.
Drawn	Scale N.T.S.
Drawn Designed	Scole N.T.S. Stotus Marked for Enquiry & Complaint log


Annex B

Project Organization Chart and Contact Detail

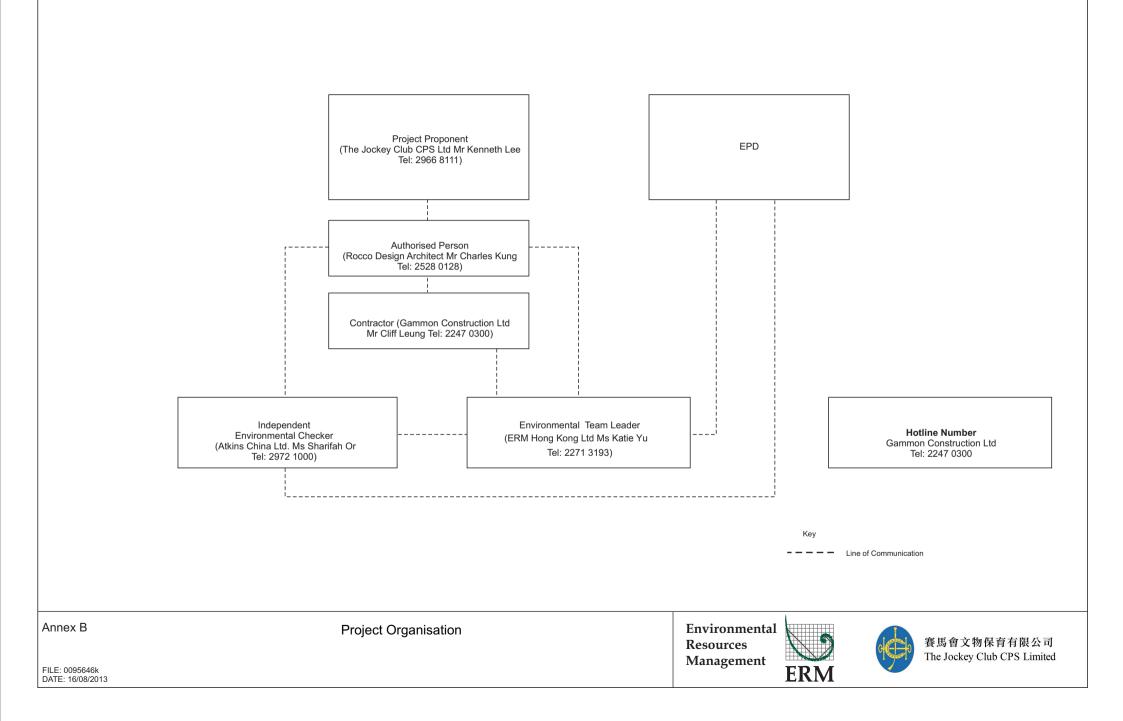

Annex C

Locations of Noise Monitoring Stations and Noise Sensitive Receivers

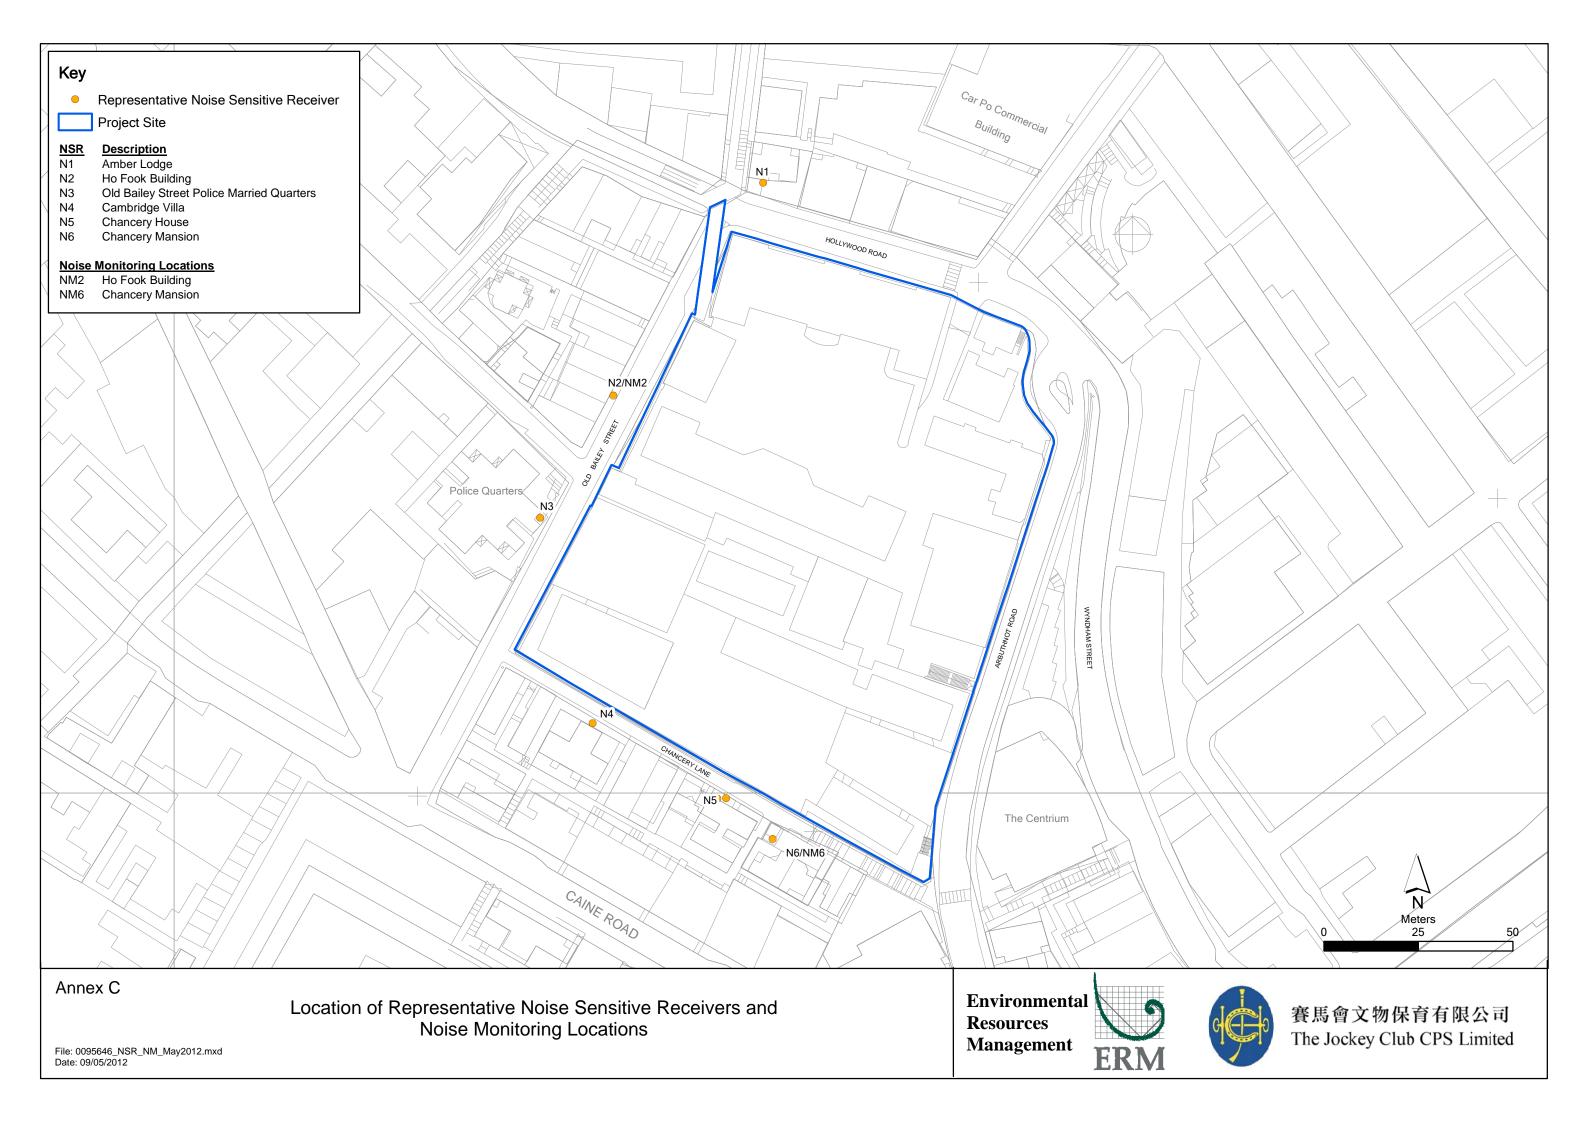

Annex D

Monitoring Schedule of the Reporting Period and Next Month

## Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - February 2016

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	01-Feb	02-Feb	03-Feb	04-Feb	05-Feb	06-Feb
		Noise Monitoring at NM2 & NM6				Noise Monitoring at NM2 & NM6
07-Feb	08-Feb	09-Feb	10-Feb	11-Feb	12-Feb	13-Feb
				Noise Monitoring at NM2 & NM6		
14-Feb	15-Feb	16-Feb	17-Feb	18-Feb	19-Feb	20-Feb
		Noise Monitoring at NM2 & NM6				
21-Feb	22-Feb	23-Feb	24-Feb	25-Feb	26-Feb	27-Feb
	Noise Monitoring at NM2 & NM6					Noise Monitoring at NM2 & NM6
28-Feb	29-Feb					

#### Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Next Reporting Month - March 2016

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		01-Mar	02-Mar	03-Mar	04-Mar	05-Mar
					Noise Monitoring at NM2 & NM6	
06-Mar	07-Mar	08-Mar	09-Mar	10-Mar	11-Mar	12-Mar
				Noise Monitoring at NM2 & NM6		
13-Mar	14-Mar	15-Mar	16-Mar	17-Mar	18-Mar	19-Mar
			Noise Monitoring at NM2 & NM6			
20-Mar	21-Mar	22-Mar	23-Mar	24-Mar	25-Mar	26-Mar
		Noise Monitoring at NM2 & NM6		Noise Monitoring at NM2 & NM6	Public Holiday	Public Holiday
27-Mar	28-Mar	29-Mar	30-Mar	31-Mar		
	Public Holiday		Noise Monitoring at NM2 & NM6			

Annex E

Calibration Reports for Calibrators and Sound Level Meters



Sun Creation Engineering Limited

Calibration and Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No. : C156917 證書編號

	TEST CONDITIONS / Temperature / 溫度 : Line Voltage / 電壓 :	(23 ± 2)°C Relative Humidity / 相對濕度 : (55 ± 20)%
-	TEST SPECIFICATIO	PNS / 測試規範
	DATE OF TEST / 測試	计期 : 15 December 2015
5	The results do not exceed The results are detailed i The test equipment used	particular unit-under-test only. d manufacturer's specification. in the subsequent page(s). for calibration are traceable to National Standards via : ne Hong Kong Special Administrative Region Standard & Calibration Laboratory / Keysight Technologies poratory, Germany
	Tested By : 測試	H T Wong Technical Officer
	Certified By : 核證	Date of Issue : 15 December 2015 K Lee 簽發日期 Project Engineer

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration and Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No. : C156917 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- 2. The results presented are the mean of 3 measurements at each calibration point.
- 3. Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C153519
CL281	Multifunction Acoustic Calibrator	DC130171
TST150A	Measuring Amplifier	C141558

- 4. Test procedure : MA100N.
- 5. Results :
- 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.1	± 0.25	± 0.2
114 dB, 1 kHz	114.1		

#### 5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	1.000 0	$1 \text{ kHz} \pm 5 \text{ Hz}$	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

#### Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration and Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No. : C156918 證書編號

	ITEM TESTED / 送檢項目 Description / 儀器名稱 : Manufacturer / 製造商 : Model No. / 型號 : Serial No. / 編號 : Supplied By / 委託者 :	( Job No. / 序引編號: IC15-2756 ) Sound Level Meter Casella CEL-633A 3521757 Envirotech Services Co. Room 113, 1/F, My Loft, 9 Hoi Wing New Territories, Hong Kong	Date of Receipt / 收件日期:4 December 2015 Road, Tuen Mun,	
	TEST CONDITIONS / 測討	《條件		-
	Temperature / 溫度 : (23 Line Voltage / 電壓 :	5 ± 2)°C	Relative Humidity / 相對濕度 : (55 ± 20)%	
	TEST SPECIFICATIONS / Calibration check DATE OF TEST / 測試日期			
-		cular unit-under-test only. nufacturer's specification. e subsequent page(s). calibration are traceable to National Star ong Kong Special Administrative Regio ysight Technologies ory, Germany		
	Tested By : 測試	H T Wong Technical Officer		
		1		

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

Date of Issue

簽發日期

•

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certified By

核證

K C Lee Project Engineer 15 December 2015



Sun Creation Engineering Limited Calibration and Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No.: C156918 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration using the Casella Acoustic Calibrator CEL-120/1, S/N : 3421612 was performed before the test.
- 3. The results presented are the mean of 3 measurement at each calibration point.
- 4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C150014
CL281	Multifunction Acoustic Calibrator	DC130171

- 5. Test procedure : MA101N.
- 6. Results :
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

UUT Setting		Applied Value		UUT	IEC 61672 Class 1
Time	Frequency	Level	Freq.	Reading	Spec.
Weighting	Weighting	(dB)	(kHz)	(dB)	(dB)
L <sub>F</sub>	A	114.00	1	113.9	± 1.1

#### 6.1.2<sup>s</sup> Linearity

UUT	Setting	Applied Value		UUT
Time Weighting	Frequency Weighting	Level (dB)	Freq. (kHz)	Reading (dB)
L <sub>F</sub>	A	114.00	1	113.9 (Ref.)
		104.00		103.9
		94.00		93.9

IEC 61672 Class 1 Spec. :  $\pm$  0.6 dB per 10 dB step and  $\pm$  1.1 dB for overall different.

#### 6.2 Time Weighting

UUT	Setting	Applie	d Value	UUT	IEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Spec. (dB)
L <sub>F</sub>	A	114.00	1	113.9	Ref.
Ls				113.9	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所 c/o 香港新界屯門興安里一號青山灣機樓四樓 Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab/@ suncreation.com Website/網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

## Certificate of Calibration 校正證書

Certificate No. : C156918 證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT	Setting	App	lied Value	UUT	IEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq.	Reading (dB)	Spec. (dB)
L <sub>F</sub>	A	94.00	63 Hz	87.7	$-26.2 \pm 1.5$
			125 Hz	97.7	$-16.1 \pm 1.5$
			250 Hz	105.2	$-8.6 \pm 1.4$
			500 Hz	110.6	$-3.2 \pm 1.4$
			1 kHz	113.9	Ref.
			2 kHz	115.1	$+1.2 \pm 1.6$
			4 kHz	114.8	$+1.0 \pm 1.6$
	201012018		8 kHz	112.4	-1.1(+2.1;-3.1)
			12.5 kHz	108.3	-4.3(+3.0;-6.0)

#### 6.3.2 C-Weighting

UUT	Setting	App	lied Value	UUT	IEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq.	Reading (dB)	Spec. (dB)
L <sub>F</sub>	C	94.00	63 Hz	113.0	$-0.8 \pm 1.5$
			125 Hz	113.7	$-0.2 \pm 1.0$
			250 Hz	113.9	$0.0 \pm 1.0$
			500 Hz	113.9	$0.0 \pm 1.0$
			1 kHz	113.9	Ref.
			2 kHz	113.7	$-0.2 \pm 1.0$
			4 kHz	113.0	$-0.8 \pm 1.0$
			8 kHz	110.6	-3.0 (+1.5 ; -3.0)
			12.5 kHz	106.4	-6.2 (+3.0 ; -6.0)

Remarks : - UUT Microphone Model No. : CEL-251 & S/N : 1950

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :	104 dB	1 kHz 2 kHz - 4 kHz 8 kHz 12.5 kHz : 1 kHz	: $\pm 0.45 \text{ dB}$ : $\pm 0.40 \text{ dB}$ : $\pm 0.30 \text{ dB}$ : $\pm 0.45 \text{ dB}$ : $\pm 0.45 \text{ dB}$ : $\pm 0.55 \text{ dB}$ : $\pm 0.80 \text{ dB}$ : $\pm 0.10 \text{ dB}$ (Ref. 114 dB)
	94 dB	: 1 kHz	$= \pm 0.10 \text{ dB} (\text{Ref. 114 dB})$

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

Annex F

# Event / Action Plans for Noise

## Annex F Event and Action Plan for Noise

Event				Ac	tion			
	En	vironmental Team (ET)		dependent Environmental necker (IEC)	A	uthorised Person (AP)	C	ontractor
Action Level	1. 2. 3. 4. 5.	Notify IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, AP and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness.	<ol> <li>1.</li> <li>2.</li> <li>3.</li> </ol>	Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the AP accordingly; Supervise the implementation of remedial measures.	<ol> <li>1.</li> <li>2.</li> <li>3.</li> <li>4.</li> </ol>	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to proposed remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented.	1. 2.	Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.
Limit Level	<ol> <li>1.</li> <li>2.</li> <li>3.</li> <li>4.</li> <li>5.</li> <li>6.</li> <li>7.</li> <li>8.</li> </ol>	Identify source; Inform IEC and AP; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, AP and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and AP informed of the results; If exceedance stops, cease additional monitoring.		Discuss amongst AP, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the AP accordingly; Supervise the implementation of remedial measures.	<ol> <li>1.</li> <li>2.</li> <li>3.</li> <li>4.</li> <li>5.</li> </ol>	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	<ol> <li>1.</li> <li>2.</li> <li>3.</li> <li>4.</li> <li>5.</li> </ol>	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the AP until the exceedance is abated.

Annex G

Summary of Implementation Status

## Annex G Implementation Schedule for Environmental Protection Measures

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultur	al Herita	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	No field work in the reporting month.
S3.9.2	S3.3.1	<u>Vibration Monitoring</u> A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	V
S3.9.2	S3.3.3	<u>Compliance of the Approved Measures and Auditing</u> Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement.			
		AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	<u>Archival Recording</u> An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of as- built drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	<u>General Construction Methods</u> Prior to the commencement of the modification/refurbishment works at	Whole site	During construction	$\diamond$
		an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be		consu action	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
53.7.1 & 3.7.2	-	checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings / structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the c	Whole site	During detailed design, construction, post- construction and operation	√ - CMP was implemented during the reporting month. There were no updates for the CMP.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Landsca	ipe & Visi	ıal	I		
S4.7.27		<u>In-situ Tree Protection - Cordon Zone (CZ)</u> Cordon off each tree along its drip line (below the crown) with a chain- link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m	Whole site	During construction	- Part of the cordon zone of Tree-5 has been used as a temporary storage area of construction materials. The Contractor was recommended to perform proper measures to protect Tree-5.
		from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.			
S4.7.2	-	In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.	Whole site	During construction	N/A – no root pruning has been conducted yet
S4.7.2	-	<u>In-situ Tree Protection - Foliage cleansing system</u> A sprinkler cleansing system will be installed either in the crown of the tree or at a suitable location on an adjacent building to provide the	Whole site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		means to wash the foliage of the accumulated dust when necessary,			
		particularly in the dry season.			
S4.7.2	S4	In-situ Tree Protection - Monthly inspection	Whole site	During construction	$\checkmark$
		Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau ( <i>http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf</i> ) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.			
S4.7.2	-	<u>Light Control</u> Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	$\checkmark$
S4.7.2	S4	Compensatory Tree Planting A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10. The existing tree site will be enlarged to become a wide tree strip to accommodate at least six trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil underneath so that fertilizers and conditioners could be added on a	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	N/A – Compensatory Tree Planting will be conducted at later stage.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.			
		Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. T10 has a DBH of 20 cm ( <i>Table 4.3</i> ), and it is proposed that six trees of heavy standard size be planted, each with a DBH of around 10 cm and root balls of not less than 0.75 m diameter and 0.75 m depth,. Since the aggregate DBH of the new trees would be 60 cm, the rate of compensation is equivalent to three times the DBH of T10, far beyond the requirements			
		The six replacement trees should be planted in the new tree strip in two staggered rows, maximising distance between each tree to avoid mutual interference in the future. It is recommended that the species selected should have a small final dimension of less than 10 m height given the proximity to built structures such as the retaining wall and buildings. Two each of the outstanding and related flowering tree species connected to local natural history are suggested::			
		<ul> <li>Bauhinia 'Blakeana' a native evergreen species with deep mauve flowers and an exceptionally long flowering period from late autumn to early spring.</li> </ul>			
		<ul> <li>Bauhinia purpure, a native evergreen with lighter purple flowers from late autumn to early winter.</li> </ul>			
		<ul> <li>Bauhinia variegata, an exotic deciduous species, with pale pinkish flowers in spring to early summer often when the tree has little or no leaves.</li> </ul>			
S4.7.2	S4	Vertical Greening	Inner Southern Wall	During detailed design and	N/A – No vertical greening was conducted during the reporting month.
		Within the limitations of the conservation of the CPS character, greening of vertical structures should be provided where possible.		construction	
		As such it is recommended that the inner southern wall of the Site be planted as a green wall. The plantings should be inserted in between each of the large protruding piers and an offset be made from both the			

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		top and bottom edge so that old and new are equally visible. An independent frame should be strategically positioned in order to ensure minimal disturbance to the original wall, and provide the main structural support and planting surface for the green wall. The frame on to which the new green will be planted should contain its own irrigation system so that moisture for the plants will remain mainly on the planting surface and not the exiting wall behind. The planting chosen should be appropriate to the Hong Kong climate, requiring relatively little maintenance to sustain the quality of both plants and wall.			
S4.7.2	-	<u>New Custom Paving</u> New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A – No custom paving was conducted during the reporting month.
S4.7.2	S4	<u>In-situ Tree Protection - Quarterly inspection</u> Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction.	Whole site	During post construction and operation	N/A – The quarterly inspection will be conducted at later stage.
Noise			•		
<i>S5.9</i>	-	<ul> <li>The following site practices should be followed during the construction of the Project:</li> <li>Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase;</li> <li>Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase;</li> <li>Mobile plant, if any, will be sited as far away from NSRs as possible;</li> </ul>	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		<ul> <li>Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum;</li> <li>Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>			
<i>\$5.9</i>	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	$\checkmark$
<i>S5.9</i>	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m <sup>-2</sup> and have no openings or gaps.	Whole Site	During construction	√
<i>S5.9</i>	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	$\checkmark$
<i>S5.9</i>	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	$\checkmark$
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	V
Air Qu	ality				
S6.8.1	-	Dust control measures stipulated in the <i>Air Pollution Control</i> ( <i>Construction Dust</i> ) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	V
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	√ 
S6.8.1	-	Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	√ 
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	$\checkmark$
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if required, from the ground floor level of building for construction of superstructure of the new buildings.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	√
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A – Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	$\checkmark$
Water (	Quality			1	
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	$\checkmark$
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A – Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	$\checkmark$
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	$\checkmark$
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	۸ 
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A – Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A – Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	$\checkmark$
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	$\checkmark$
Waste I	Manageme	nt			
S8.5	S6.3.1 & Table 6.1	<u>General</u> The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	$\checkmark$
S8.5	-	<u>Management of Waste Disposal</u> The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	N
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor.	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	√
S8.5	S6.3	<u>Reduction of Construction Waste Generation</u> C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	$\checkmark$
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	$\checkmark$
S8.5	S6	<ul> <li>Containers used for storage of chemical waste shall:</li> <li>Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;</li> <li>Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and</li> <li>Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>.</li> </ul>	Whole Site	During construction and operation	$\checkmark$
S8.5	S6	<ul> <li>Storage areas for chemical waste shall:</li> <li>Be clearly labelled and used solely for the storage of chemical waste;</li> <li>Be enclosed on at least 3 sides;</li> <li>Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest;</li> <li>Have adequate ventilation;</li> <li>Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and</li> <li>Be arranged so that incompatible materials are appropriately separated.</li> </ul>	Whole Site	During construction and operation	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	$\checkmark$
S8.5	S6 & Table 6.1	<u>General Refuse</u> General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	$\checkmark$
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	$\checkmark$
S8.5	S6	<u>Staff Training</u> At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	$\checkmark$
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	√

Remark:

 $\sqrt{}$  Compliance of Mitigation Measures

<> Compliance of Mitigation but need improvement

x Non-compliance of Mitigation Measures

▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd

Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd

N/A Not Applicable in Reporting Period

Annex H

Noise Monitoring Results

#### Annex H Noise Monitoring Results


#### Daytime Noise Monitoring Results


#### NM6 Chancery Mansion

Date	Start Time	End Time	Weather	Noise	level (dB(A)	), 30 min	Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90		Observed				
02-Feb-16	10:47	11:17	Cloudy	65.7	67.6	63.1	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
06-Feb-16	8:30	9:00	Sunny	61.9	63.9	59.3	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
11-Feb-16	9:00	9:30	Cloudy	63.9	65.7	61.1	-	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
16-Feb-16	9:00	9:30	Cloudy	65.7	67.1	64.2	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
22-Feb-16	9:47	10:17	Cloudy	68.9	70.9	66.9	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
27-Feb-16	8:35	9:05	Cloudy	68.0	69.4	64.7	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	61.9								
			Max.	68.9								

#### NM2 Ho Fook Building

				Noise	level (dB(A)	), 30 min	Major Construction Noise	Other Noise		Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Source(s) Observed	Source(s) Observed	Remarks	(m/s)	Model / ID	Model / ID
02-Feb-16	10:09	10:39	Cloudy	67.0	70.7	64.1	Interior fitting (within the project site)	Traffic noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
06-Feb-16	10:23	10:53	Sunny	67.1	71.0	58.8	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
11-Feb-16	9:39	10:09	Cloudy	55.6	57.5	52.9	-	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
16-Feb-16	11:00	11:30	Cloudy	68.6	71.0	65.1	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
22-Feb-16	10:30	11:00	Cloudy	71.5	74.2	66.7	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
27-Feb-16	9:13	9:43	Cloudy	70.7	72.7	66.8	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
	•		Min.	55.6								
			Max.	71.5								

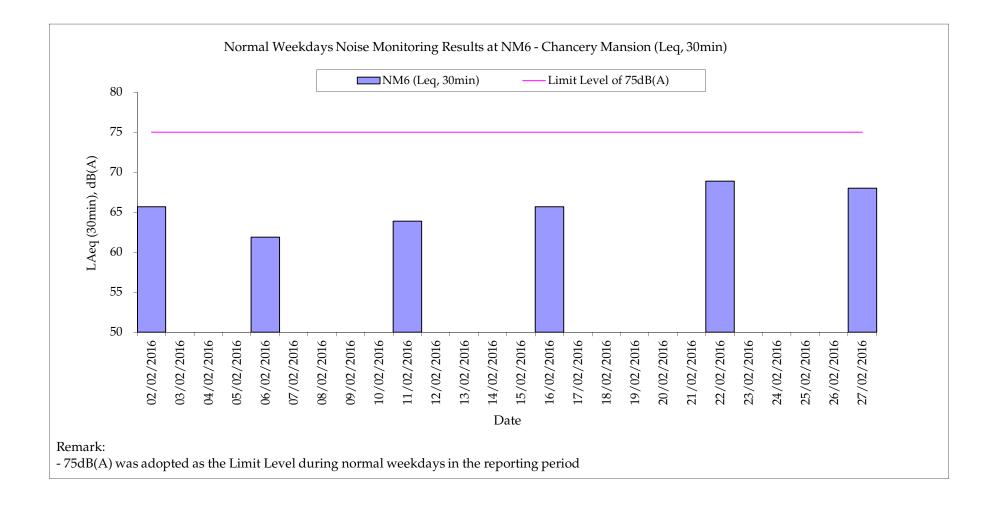

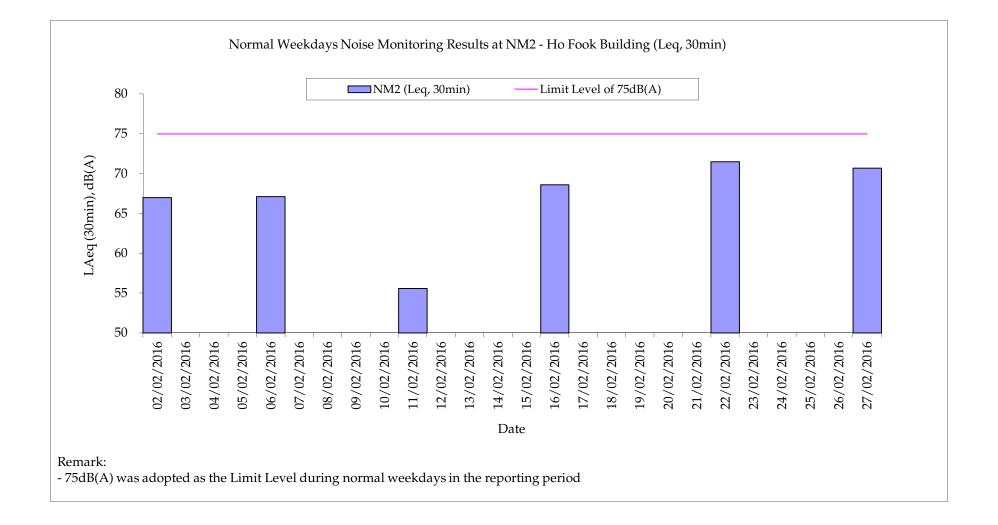

Annex I

Construction Programme for the Project

Activity	Activity	Dur	Forecast	Forecast	SA Programme	SA Programme	2015 2016 2017 2018
ID	Description	Calendar Days	Start	Finish	Planned Start	Planned Finish	
EXISTING	BUILDINGS (BA14)	Duys					
Block 1							
01010			03OCT12A	18MAR16	03OCT12*	31JUL15	
01030	REMAIN WORK & POST BA14 INSPECTION WORK	135	19MAR16	31JUL16			
Block 2 02010	BLOCK 2 - ARMOURY & STORE	870	04MAY13A	22MAR16	03MAY13*	19SEP15	
02020	REMAIN WORK & POST BA14 INSPECTION WORK		23MAR16	21JUN16			
Block 3							
03010	BLOCK 3 - BARRACK BLOCK	1,067	21MAR13A	06APR16	21MAR13*	20FEB16	
03020	REMAIN WORK&POST BA14 INSPEC WORK INCL A&A	144 (	07APR16	28AUG16			
Block 4							
04010	BLK 4-DORM BLKA&B (SEE SEPARATE PROGRAMME SUBM)	963	12AUG13A	06OCT16	12AUG13*	31MAR16	
Block 6							
06010	BLOCK 6 - DORMITORY BLOCK C		18FEB13A	04MAR16	18FEB13*	26SEP15	
06020	REMAIN WORK & POST BA14 INSPECTION WORK	112	05MAR16	24JUN16			
Block 7 07010	BLOCK 7 - DORMITORY BLOCK D	202	19MAR13A	03MAR16A	19MAR13*	02SEP15	
07010	REMAIN WORK & POST BA14 INSPECTION WORK		03MAR16	25JUN16			REMAIN WORK & POST BA14 INSPECTION WORK
				20001110			
Block 9 09010	BLOCK 9 - CENTRAL MAGISTRACY	948	17JUN13A	30JUN16	17JUN13*	20JAN16	BLOCK 9 - CENTRAL MAGISTRACY
Block 10							
10010	BLOCK 10 - SUPERINTENDENT HOUSE	1,059	11JAN13A	02APR16	11JAN13*	05DEC15	
10020	REMAIN WORK&POST BA14 INSPECT WORK INCL BALCONY	108	03APR16	19JUL16			
Block 11							
11010	BLOCK 11 - A HALL	1,069	10NOV12A	30MAR16	10NOV12*	14OCT15	
11020	REMAIN WORK & POST BA14 INSPECTION WORK	83 :	31MAR16	21JUN16			REMAIN WORK & POST BA14 INSPECTION WORK
Block 12		1 000					
12010	BLOCK 12 - B HALL REMAIN WORK & POST BA14 INSPECTION WORK		10NOV12A	06APR16	10NOV12*	250CT15	
12020	REMAIN WORK & POST BAT4 INSPECTION WORK	78	07APR16	23JUN16			
Block 19 19010	BLOCK 19	798	01AUG13A	19MAR16	01AUG13*	07OCT15	
19020	REMAIN WORK & POST BA14 INSPECTION WORK		20MAR16	30APR16			
EVTEDN	AL WORKS						
ST060	REMAINING HARD & SOFT LANDSCAPING	97	03MAR16*	07JUN16	18DEC15*	26APR16	REMAINING HARD & SOFT LANDSCAPING
ST065	RESIDUAL WORKS	37	08JUN16	14JUL16	27APR16	31MAY16	
NON-OP	BUILDINGS CLOSE OUT ACTIVITIES						
EXCEPT	BLOCK 4 & 9						
ST130	MOE PAVING EXCEPT BLK 4 & 9		24SEP15A	25FEB16A	15SEP15*	17DEC15	
ST135	REMAIN MOE PAVING EXCEPT BLK 4 & 9		26FEB16A	12APR16			REMAIN MOE PAVING EXCEPT BLK 4 & 9
ST140	TEST & COMMISSION FOR FSI (EXCEPT BLK 4 & 9)		21DEC15A	26FEB16A	01SEP15*	18DEC15	
ST150	SUBMIT F251/314A TO FSD (EXCEPT BLK 4 & 9)	0	10MAR16		18DEC15		
tart Date inish Date			07J	IAR12 S6C1		CENTRAL POLIC	CE STATION Sheet 1 of 2 IENT PROGRAMME FOR NON-OP
lata Date Iun Date			03M 07MAR16	IAR16		BUILDIN & FOOTBR	
					(WITH		G OF 03 MAR 2016)
	?Primavera Systems, Inc.						
			_				

Activi	ty Activity	Dur	Forecast	Forecast	SA Programme	SA Programme	2015	2016	2017	2018
ID	Description	Calendar		Finish	Planned Start	Planned Finish	A S O N D J F	M A M J J A S O N D	J F M A M J J A S O N I	J F M A M J J A
ST205	SUBMIT FORM BA14 (EXCEPT BLK 4 & 9)	Days (	12APR16		20JAN16				<pre></pre>	
BLOCK	9									
ST370	MOE PAVING BLK 9	45	29MAR16	12MAY16				MOE PAVING BLK 9		
ST380	TEST & COMMISSION FOR FSI (BLK 9)	45	29MAR16	12MAY16				TEST & COMMISSION FOR FSI	(вьк'я)	
ST390	SUBMIT F251/314A TO FSD (BLK 9)	(	13MAY16					SUBMIT F251/314A TO FSD (B	LK 9)	
ST410	SUBMIT FORM BA14 (BLK 9)	0	15JUN16						(9)	
BLOCK	4									
ST265	MOE PAVING BLK 4 TENTATIVE	45	04JUL16	17AUG16	30JAN16	14MAR16			4 TENTATIVE	
ST270	TEST & COMMISSION FOR FSI (BLK 4) TENTATIVE	21	28JUL16	17AUG16	23FEB16	14MAR16			NON FOR FSI (BLK 4) TENTATIVE	
ST280	SUBMIT F251/314A TO FSD (BLK 4) TENTATIVE	(	18AUG16		15MAR16			■ F=SUBMIT F251/31/	4A TO FSD (BLK 4) TENTATIVE	
ST300	SUBMIT FORM BA14 (BLK 4) TENTATIVE	(	20SEP16		16APR16			Г=	RM BA14 (BLK 4) TENTATIVE	
ST360	PRACTICAL COMPLETION (BLK 4)	(		06OCT16					AL COMPLETION (BLK 4)	
INSPEC	TION & HANDOVER									
ST320	HANDOVER INSEPCTIONS, RECTIFICATION & HANDOVER	77	27MAR16	11JUN16	03FEB16	26APR16		HANDOVER INSEPCTIONS,	RECTIFICATION & HANDOVER(EXCEPT BLOCK 4	8 9)
ST323	ISSUE FR & FL WATER CERTIFICATE	(	)	15JUN16				ISSUE FR & FL WATER CI		
ST326	BA14 ACKNOWLEDGEMENT	(	)	15JUN16					NT	
ST330	PACTICAL COMPLETION FOR NON-OP BLDGS	(		15JUN16		26APR16			FOR NON-OP BLDGS (EXCEPT BLOCK 4 & 9)	
ST335	HANDOVER INSPECTION, RECTIFICATION/HANDOVER (B9)	43	30JUN16*	11AUG16					CTION, RECTIFICATION/HANDOVER (B9)(BLOCK	9)
FOOTBR	RIDGE									
ST340	UTILITIES DIVERS'N/PILING/DECK STRUCT/FINISHES	791	26FEB15A	07JUN17	26FEB15*	26APR17				G/DECK STRUCT/FINISHES
ST350	PRACTICAL COMPLETION FOR FOOTBRIDGE	(		07JUN17		26APR17		ETION FOR FOOTBRIDGE(Footbridge progr	amme to be reviewed)	

Start Date 15MAR	CENTRAL FOLIGE STATION		GCL/P/J3416/SA5/SUM/NOP
Finish Date 07JUN	SUMMARY SUPPLEMENTAL AGREEMENT PROGRAMME FOR NON-OP		Date Revision Checked Approved
Data Date			
Run Date 07MAR16 13:	& FOOTBRIDGE		
		Gammon	
	(WITH PROGRESS AS OF 03 MAR 2016)		
?Primavera Systems, Inc.			

OP ESSENTIALS         CENTRAL BASEMENT PLANT ROOM         01020       CENTRAL BASEMENT PLANT ROOM         BLOCK 8         08010       BLOCK 6 - ABLUTIONS BLOCK         08020       (FUEL TANK) DG INSPECTION COMPLETE         08050       DG INSPECTION COMPLETE         08080       TESTED & COMMISISONED FOR FS INSPECTION         08085       POST OP INSPECT WORK-MOBILE CHILLER SWITCHBO         BUILDING A         08070       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HECK         SW010         DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW010         DRAIN/TERMINAL MANHOLE CONNECT HOLLYW RD         SW010         DRAIN/TERMINAL MANHOLE CONNECT HOLLYW RD         SW025         COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYW         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW025         COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW025         COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW025         COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.	DARD	1,046 04OCT1 1,259 23APR1 4 17SEP1 0 0 70 27APR1 0 22MAY1 0	2A 19MAR16 5A 24SEP15A 24SEP15A 05JAN16A 6* 05JUL16 5A 12JUN15A	04OCT12* 23APR12* 07OCT15*	27JUL15 03OCT15 10OCT15 10OCT15 18DEC15*	CENTRAL BASEMENT PLANT ROOM BLOCK 8 - ABLUTIONS BLOCK FUEL TANK) DG INSPECTION COMPLETE OG INSPECTION COMPLETE TESTED & COMMISISONED FOR FS INSPECTIONMILESTONE ALS AND SITE
01020       CENTRAL BASEMENT PLANT ROOM         BLOCK 8       08010       BLOCK 8 - ABLUTIONS BLOCK         08020       (FUEL TANK) DG INSPECTION COMPLETE         08050       DG INSPECTION COMPLETE         08080       TESTED & COMMISISONED FOR FS INSPECTION         08080       TESTED & COMMISISONED FOR FS INSPECTION         08080       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HECK         SITEWIDE SERVICES         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW026       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW027       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW028       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT	DARD	1,259 23APR1 4 17SEP1 0 0 70 27APR1	2A 19MAR16 5A 24SEP15A 24SEP15A 05JAN16A 6* 05JUL16 5A 12JUN15A	23APR12* 07OCT15*	03OCT15 10OCT15 10OCT15	CENTRAL BASEMENT PLANT ROOM
BLOCK 8         08010       BLOCK 8 - ABLUTIONS BLOCK         08020       (FUEL TANK) DG INSPECTION COMPLETE         08050       DG INSPECTION COMPLETE         08080       TESTED & COMMISISONED FOR FS INSPECTION         08080       TESTED & COMMISISONED FOR FS INSPECTION         08080       POST OP INSPECT WORK-MOBILE CHILLER SWITCHBO         BUILDING A       08060         08070       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HED         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW015       COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYW         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW0	DARD	1,259 23APR1 4 17SEP1 0 0 70 27APR1	2A 19MAR16 5A 24SEP15A 24SEP15A 05JAN16A 6* 05JUL16 5A 12JUN15A	23APR12* 07OCT15*	03OCT15 10OCT15 10OCT15	BLOCK 8 - ABLUTIONS BLOCK      (FUEL TANK) DG INSPECTION COMPLETE      ODG INSPECTION COMPLETE
08010       BLOCK 8 - ABLUTIONS BLOCK         08020       (FUEL TANK) DG INSPECTION COMPLETE         08050       DG INSPECTION COMPLETE         08080       TESTED & COMMISISONED FOR FS INSPECTION         08085       POST OP INSPECT WORK-MOBILE CHILLER SWITCHBO <b>BUILDING A</b> 08060         08070       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HECK         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW021       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT	DARD	4 17SEP1 0 0 70 27APR1	5A 24SEP15A 24SEP15A 05JAN16A 6* 05JUL16 5A 12JUN15A	07OCT15*	100CT15 100CT15	
08020       (FUEL TANK) DG INSPECTION COMPLETE         08050       DG INSPECTION COMPLETE         08080       TESTED & COMMISISONED FOR FS INSPECTION         08085       POST OP INSPECT WORK-MOBILE CHILLER SWITCHBO         BUILDING A       08060         08070       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HECK         SITEWIDE SERVICES         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       COMPLETE EVA & MOES PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOES PAVING         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW	DARD	4 17SEP1 0 0 70 27APR1	5A 24SEP15A 24SEP15A 05JAN16A 6* 05JUL16 5A 12JUN15A	07OCT15*	100CT15 100CT15	
08050       DG INSPECTION COMPLETE         08080       TESTED & COMMISISONED FOR FS INSPECTION         08085       POST OP INSPECT WORK-MOBILE CHILLER SWITCHBO         BUILDING A         08060       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HEORED SUTEWIDE SERVICES         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW015       COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW021       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW021       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F & WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CER	C)	0 0 70 27APR1	24SEP15A 05JAN16A 6* 05JUL16 5A 12JUN15A		10OCT15	
08080       TESTED & COMMISISONED FOR FS INSPECTION         08085       POST OP INSPECT WORK-MOBILE CHILLER SWITCHBO         BUILDING A       08060       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HEC         SITEWIDE SERVICES         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW015       COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYW         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW026       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW027       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW028       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW029       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW0210       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW022       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTI	C)	70 27APR1	05JAN16A 6* 05JUL16 5A 12JUN15A			
08085       POST OP INSPECT WORK-MOBILE CHILLER SWITCHBO         BUILDING A       08060       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HED         SITEWIDE SERVICES         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW015       COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       COMPLETE EVA & MOES PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOES PAVING         DBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFFT COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT	C)		6* 05JUL16 5A 12JUN15A			
08060       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HEC         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW015       COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYW         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       COMPLETE EVA & MOES PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOES PAVING		0 22MAY1 0	5A 12JUN15A			
08060       DEMOLITION OF BLDG A         08070       DEMOLITION OF BLDG A COMPLETE (SUBJECT TO HEC         SITEWIDE SERVICES         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW015       COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYW         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       COMPLETE EVA & MOES PAVING FOR FS INSPECTION         EW010       COMPLETE REMAINING MOES PAVING         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW015		0 22MAY: 0				APR 2015 TO DATA
SITEWIDE SERVICES         SW010       DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RD         SW015       COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYW         SW020       DRAIN/TERMINAL MANHOLE CONNECT OLD B. ST         SW025       COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.         SW030       BARRACK LANE (ZONE L3 AREA 2) SERVICES         SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       COMPLETE EVA & MOES PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOES PAVING         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFFT COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT		0		02MAY15*	06JUL15	
SW010DRAIN/TERMINAL MANHOLE CONNECT HOLLYWD RDSW015COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYWSW020DRAIN/TERMINAL MANHOLE CONNECT OLD B. STSW025COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.SW026DRAIN/TERMINAL MANHOLE CONNECT OLD B.SW027COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.SW028BARRACK LANE (ZONE L3 AREA 2) SERVICESSW040MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICESSW045OTHER REMAINING SITEWIDE SERVICESSW050F S WATER CONNECTION & ISSUE WATER CERTIFICATSW060FR&FL WATER CONNECTION & ISSUE WATER CERTIFICEVA & MOE PAVINGEW010COMPLETE EVA & MOES PAVING FOR FS INSPECTIONEW020COMPLETE REMAINING MOES PAVINGOBW010OLD BAILEY WING (EXCEPT POST OP FIT OUT)OBW013MAIN R/F STRUCT SLAB/ROOFLIGHT SUFFT COMPLETOBW015TESTED & COMMISSIONED FOR FS INSPECTIONOBW020OLD BAILEY WING POST OP FIT OUT	ND RD		12JUN15A		06JUL15	
SW015COMPL DRAIN/TERMINAL MANHOLE CONNECT HOLLYVSW020DRAIN/TERMINAL MANHOLE CONNECT OLD B. STSW025COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.SW030BARRACK LANE (ZONE L3 AREA 2) SERVICESSW040MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICESSW045OTHER REMAINING SITEWIDE SERVICESSW050F S WATER CONNECTION & ISSUE WATER CERTIFICATSW060FR&FL WATER CONNECTION & ISSUE WATER CERTIFICATSW060FR&FL WATER CONNECTION & ISSUE WATER CERTIFICATSW060FR&FL WATER CONNECTION & ISSUE WATER CERTIFICATSW060COMPLETE EVA & MOES PAVING FOR FS INSPECTIONEW010COMPLETE REMAINING MOES PAVINGEW020COMPLETE REMAINING MOES PAVINGOBW010OLD BAILEY WING (EXCEPT POST OP FIT OUT)OBW013MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLETOBW015TESTED & COMMISSIONED FOR FS INSPECTIONOBW020OLD BAILEY WING POST OP FIT OUT	ND RD					
SW020DRAIN/TERMINAL MANHOLE CONNECT OLD B. STSW025COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.SW030BARRACK LANE (ZONE L3 AREA 2) SERVICESSW040MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICESSW045OTHER REMAINING SITEWIDE SERVICESSW050F S WATER CONNECTION & ISSUE WATER CERTIFICATSW060FR&FL WATER CONNECTION & ISSUE WATER CERTIFICEVA & MOE PAVINGEW010COMPLETE EVA & MOE's PAVING FOR FS INSPECTIONEW020COMPLETE REMAINING MOE's PAVINGNEW BUILDINGS & OP EXISTING BUILDINGSOBWOBW010OLD BAILEY WING (EXCEPT POST OP FIT OUT)OBW013MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLETOBW015TESTED & COMMISSIONED FOR FS INSPECTIONOBW020OLD BAILEY WING POST OP FIT OUT	WD RD	105 05MAR1	5A 14AUG15A	05MAR15*	17JUN15	
SW025COMPL DRAIN/TERMINAL MANHOLE CONNECT OLD B.SW030BARRACK LANE (ZONE L3 AREA 2) SERVICESSW040MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICESSW045OTHER REMAINING SITEWIDE SERVICESSW050F S WATER CONNECTION & ISSUE WATER CERTIFICATSW060FR&FL WATER CONNECTION & ISSUE WATER CERTIFICATSW060FR&FL WATER CONNECTION & ISSUE WATER CERTIFICATSW060COMPLETE EVA & MOES PAVING FOR FS INSPECTIONEW010COMPLETE REMAINING MOES PAVINGEW020COMPLETE REMAINING MOES PAVINGNEW BUILDINGS & OP EXISTING BUILDINGSOBWOBW010OLD BAILEY WING (EXCEPT POST OP FIT OUT)OBW015TESTED & COMMISSIONED FOR FS INSPECTIONOBW020OLD BAILEY WING POST OP FIT OUT		0	14AUG15A		17JUN15	
SW030BARRACK LANE (ZONE L3 AREA 2) SERVICESSW040MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICESSW045OTHER REMAINING SITEWIDE SERVICESSW050F S WATER CONNECTION & ISSUE WATER CERTIFICATSW060FR&FL WATER CONNECTION & ISSUE WATER CERTIFICEVA & MOE PAVINGEW010COMPLETE EVA & MOEs PAVING FOR FS INSPECTIONEW020COMPLETE REMAINING MOEs PAVINGNEW BUILDINGS & OP EXISTING BUILDINGSOBWOBW010OLD BAILEY WING (EXCEPT POST OP FIT OUT)OBW013MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLETOBW015TESTED & COMMISSIONED FOR FS INSPECTIONOBW020OLD BAILEY WING POST OP FIT OUT		137 09APR1	5A 29JUL15A	09APR15*	23AUG15	DRAIN TERMINAL MANHOLE CONNECT OLD B. ST
SW040       MIDDLE PLATFORM (ZONE M5) - REMAIN SERVICES         SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFIC         EVA & MOE PAVING         EW010       COMPLETE EVA & MOEs PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOEs PAVING         NEW BUILDINGS & OP EXISTING BUILDINGS         OBW         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT	ST	0	29JUL15A		23AUG15	
SW045       OTHER REMAINING SITEWIDE SERVICES         SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFIC         EVA & MOE PAVING         EW010       COMPLETE EVA & MOEs PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOEs PAVING         NEW BUILDINGS & OP EXISTING BUILDINGS         OBW         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT		133 17JUN1	5A 27FEB16A	17JUN15*	29OCT15	BARRACK LANE (ZONE L3 AREA 2) SERVICES
SW050       F S WATER CONNECTION & ISSUE WATER CERTIFICAT         SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFIC         EW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFIC         EW010       COMPLETE EVA & MOEs PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOEs PAVING         NEW BUILDINGS & OP EXISTING BUILDINGS         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT		119 22JUL1	5A 12JAN16A	30JUN15*	08NOV15	MIDDE PLATFORM (ZONE M5) - REMAIN SERVICES
SW060       FR&FL WATER CONNECTION & ISSUE WATER CERTIFIC         EVA & MOE PAVING         EW010       COMPLETE EVA & MOES PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOES PAVING         NEW BUILDINGS & OP EXISTING BUILDINGS         OBW         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT		281 01FEB1	5A 03FEB16A	01FEB15*	08NOV15	
EVA & MOE PAVING         EW010       COMPLETE EVA & MOEs PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOEs PAVING         NEW BUILDINGS & OP EXISTING BUILDINGS         OBW         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT	E	81 26FEB1	6A 11MAY16	30OCT15*	26NOV15	F S WATER CONNECTION & ISSUE WATER CERTIFICATE
EW010       COMPLETE EVA & MOES PAVING FOR FS INSPECTION         EW020       COMPLETE REMAINING MOES PAVING         NEW BUILDINGS & OP EXISTING BUILDINGS         OBW         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT	CATE	77 31MAR1	6* 15JUN16	07NOV15*	04DEC15	
EW020       COMPLETE REMAINING MOEs PAVING         NEW BUILDINGS & OP EXISTING BUILDINGS         OBW         OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT						
NEW BUILDINGS & OP EXISTING BUILDINGS         OBW       OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT		112 24SEP1		15AUG15*	17DEC15	
OBW           OBW010         OLD BAILEY WING (EXCEPT POST OP FIT OUT)           OBW013         MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET           OBW015         TESTED & COMMISSIONED FOR FS INSPECTION           OBW020         OLD BAILEY WING POST OP FIT OUT		46 27FEB1	6A 12APR16			
OBW010       OLD BAILEY WING (EXCEPT POST OP FIT OUT)         OBW013       MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLET         OBW015       TESTED & COMMISSIONED FOR FS INSPECTION         OBW020       OLD BAILEY WING POST OP FIT OUT						
OBW015 TESTED & COMMISSIONED FOR FS INSPECTION OBW020 OLD BAILEY WING POST OP FIT OUT		1,346 30MAR1	2A 25FEB16A	30MAR12*	05DEC15	DLD BAILEY WING (EXCEPT POST OP FIT OUT)
OBW020 OLD BAILEY WING POST OP FIT OUT	E	0	02DEC15A		16NOV15	MAIN R/F STRUCT SLAB/ROOFLIGHT SUFF'T COMPLETEMilestone MS6 (affected by AHU design change)
		0	26FEB16A		18DEC15*	
OBW025 B50 AHU running/provide climatic control-Gallery		42 27APR1	6* 07JUN16	03FEB16	15MAR16	
		0 28MAR1	6*	02DEC15*		B50 AHU running/provide climatic control-GalleryMillestone MS7 (affected by AHU design change)
OBW030 FINAL TESTING & COMMISSIONING		42 01MAY1	6 11JUN16	16MAR16	26APR16	
OBW035 REMAIN WORK&OTHER POST OP INSPECT WORK INCL	L R54	200 26FEB1	6A 12SEP16			
AW						
AW010 ARBUTHNOT WING (EXCEPT POST OP FIT OUT)		1,293 08MAY1	2A 25FEB16A	08MAY12*	21NOV15	
AW013 RAKED SEATING-COMPLETE STRUCT STEEL/INSITU CO	ONC	0	20MAY15A		06JUN15	
AW015 TESTED & COMMISSIONED FOR FS INSPECTION		0	05JAN16A		18DEC15*	TESTED & COMMISSIONED FOR FS INSPECTIONMIEstone FS-2
AW020 ARBUTHNOT WING POST OP FIT OUT		42 27APR1	6* 07JUN16	03FEB16	15MAR16	
Start Date Finish Date	I		15MAR12 S6C1 07JUN17			
Data Date Run Date		071	03MAR16 IAR16 13:16	FOR ESSENTIA	ALS & OP BUILI	
						Gammon
?Primavera Systems, Inc.						

Activit ID	y Activity Description	Dur Forecast Calendar Start	Forecast Finish	SA Programme Planned Start	SA Programme Planned Finish	2015         2016         2017         2018         2019           A         S         O         N         D         J         F         M         A         S         O         N         D         J         F         M         A         S         O         N         D         J         F         M         A         M         J         J         A         S         O         N         D         J         F         M         A         M         J         J         A         S         O         N         D         J         F         M         A         M         J         J         A         S         O         N         D         J         F         M         A         M         J         J         A         S         O         N         D         J         F         M         A         M         J         J         A         S         O         N         D         J         F         M         A         M         J         J         A         S         O         N         D         J         F         M         M         J         J         A
U	Description	Days	FINISN	Planned Start	Planned Finish	
AW030	FINAL TESTING & COMMISSIONING	42 01MAY16	11JUN16	16MAR16	26APR16	
AW035	REMAIN WORK&OTHER POST OP INSPECT WORK	173 26FEB16A	16AUG16			
BLOCK 1	3					
13010	BLOCK 13 - C HALL	1,043 18JAN13A	15APR16	18JAN13*	26NOV15	
13020	BLOCK 13-TESTED & COMMISISONED FOR FS INSPECT'N	0	05JAN16A		18DEC15*	BLOCK 13-TESTED & COMMISISONED FOR FS INSPECTINMILESTONE FS-4
13030	REMAIN WORK & POST OP INSPECTION WORK	69 16APR16	23JUN16			
BLOCK 1	4					
14010	BLOCK 14 EAST WING D HALL	1,135 220CT12A	14APR16	22OCT12*	30NOV15	BLOCK 14 EAST WING D HALL147525-025
14020	BLOCK 14 WEST WING D HALL	1,067 08JAN13A	07APR16	08JAN13*	10DEC15	
14030	BLOCK 14-TESTED & COMMISISONED FOR FS INSPECT'N	0	02MAR16*		18DEC15*	BLOCK 14-TESTED & COMMISISONED FOR FS INSPECT'NMilestone FS-5
14040	REMAIN WORK & POST BA14 INSPECTION WORK	72 15APR16	25JUN16			
BLOCK 1 15010	5 BLOCK 15 - E HALL	876 10JUN13A	08MAR16	10JUN13*	02NOV15	
		876 TUJUNT3A		10301013		
15020	BLOCK 15-TESTED & COMMISSIONED FOR FS INSPECT'N	0	02MAR16*		18DEC15*	BLOCK 15-TESTED & COMMISSIONED FOR FS INSPECT'NMilestone FS-6
15030	REMAIN WORK & POST BA14 INSPECTION WORK	77 09MAR16	24MAY16			
BLOCK 1	17					
17010	BLOCK 17 - F HALL	1,241 02MAY12A	18MAR16	02MAY12*	24SEP15	
17020	BLOCK 17-TESTED & COMMISSIONED FOR FS INSPECT'N	0	02MAR16*		18DEC15*	BLOCK 17-TESTED & COMMISSIONED FOR FS INSPECT'NMilestone FS-7
17030	REMAIN WORK & POST BA14 INSPECTION WORK	67 19MAR16	24MAY16			
FXTERN	AL WORKS					
ST060	REMAINING HARD & SOFT LANDSCAPING	97 03MAR16*	07JUN16	18DEC15*	26APR16	
ST065	RESIDUAL WORKS	37 08JUN16	14JUL16	27APR16	31MAY16	
	DINGS CLOSE OUT ACTIVITIES					
ST050	TESTING&COMMISSIONING FOR FS INSPECT (OP BLDGS)	44 21DEC15A	26FEB16A	01SEP15*	18DEC15	TESTING&COMMISSIONING FOR FS INSPECT (OP BLDGS)
ST055	SUBMIT FORM 501 (OP BLDGS)	0 26FEB16A		18DEC15		SUBMIT FORM 501 (OP BLDGS)Milestone FS-1 to 7
ST075	SUBMIT FORM BA13 TO BD	0 12APR16		20JAN16		
					00000010	
ST090	HANDOVER INSPECTIONS, RECTIFICATION & HANODVER	77 27MAR16*	11JUN16	03FEB16	26APR16	
ST093	ISSUE FR & FL WATER CETIFICATE	0	15JUN16*			
ST096	ISSUE OP	0	15JUN16			
	PRACTICAL COMPLETION	0	15JUN16		26APR16	

Start Date Finish Date Data Date Run Date

CENTRAL POLICE STATION SUMMARY SUPPLEMENTAL AGREEMENT PROGRAMME FOR ESSENTIALS & OP BUILDINGS, BLOCK 14, 15 & 17 (WITH PROGRESS AS OF 03 MAR 2016)

15MAR12 S6C1 07JUN17 03MAR16 07MAR16 13:16



	GCL/P/J3416/SA5/SUM/OP			
	Date	Revision	Checked	Approved
non				

Annex J

Tree Inspection Reports



RECEIVED 07 MAR 2016

# ₩欣榮(香港)環境管理有限公司

#### Yan Wing (Hong Kong) Environment Management Limited

香港 新界 沙頭角 新樓街 15號 二樓

No. 15, San Lau Street, 1/F., Sha Tau Kok, N.T., Hong Kong

Tel: 9776 1987, 2486 2317 Fax: 2482 4667 E-mail: yanwinghk@netvigator.com

Our Ref. : YW/TP/GAMMON/2016/2/1

2<sup>nd</sup> Mar. 2016

Tel. 2516 8823 Fax.2516 6260

Gammon Construction Limited 28/F Devon House, TaiKoo Place 979 King's Road Hong Kong

Attn : Mr. Cliff C.H. LEUNG, Ms. Oley C.T. WONG,

Dear Madam/Sir,

#### Summary of Monthly Inspection Report for the Six Existing Trees <u>at Central Police Station Compound for Feb. 2016</u> (Contract Ref. : J3416/400.4/D00025)

Tree No.	Botanical Name	Date of Inspection	Overall Health Condition Good/Fair/Poor	Remarks
Tree-5	Mangifera indica 芒果	3 <sup>rd</sup> Feb. 2016	Fair	<ol> <li>To keep monitoring on the pest disease on the tree.</li> </ol>
Tree-6	Aleurites moluccana 石栗	3 <sup>rd</sup> Feb. 2016	Fair	1. No further action is required.
Tree-7	Aleurites moluccana 石栗	3 <sup>rd</sup> Feb. 2016	Fair	1. No further action is required.
Tree-8	Plumeria rubra 紅雞蛋花	3 <sup>rd</sup> Feb. 2016	Fair	1. No further action is required.
Tree-9	Araucaria cunninghamia 花旗杉	3 <sup>rd</sup> Feb. 2016	Fair	1. No further action is required.
Tree-11	Dracaena marginata 馬尾鐵	3 <sup>rd</sup> Feb. 2016	Fair	<ol> <li>To keep monitoring on the growth of the tree.</li> </ol>





#### Yan Wing (Hong Kong) Environment Management Limited

香港 新界 沙頭角 新樓街 15 號 二樓 No. 15, San Lau Street, 1/F., Sha Tau Kok, N.T., Hong Kong

Tel: 9776 1987, 2486 2317 Fax: 2482 4667 E-mail: yanwinghk@netvigator.com

Tree Inspection Reports and Tree Group Inspection Form (Form 1) are attached for your reference and record, please.

I should be much grateful if you could endorse the attached Invoice (No.1104) and fax it to my Office at 2482 4667. Thank you.

Yours faithfully

For and on behalf of Yan Wing (HK) Environment Management Ltd.

(WONG Pak Hay) **Contract Manager** 

# FORM 1: TREE GROUP INSPECTION FORM 表格 1: 樹群檢査表格

#### General Information 基本資料

Company 公司:	Gammon Constru	uction Ltd	Name of Tree Inspection office	r 巡查人員姓名:	LAU Man Chung
File Ref. 檔案編號:	YW/TP/GAMMON	/2016/2/2	Name of Endorsement Officer	覆核人員姓名:	WONG Pak Hay
Date of Inspection 巡查		3, 2016			
Project/Contract No.合	約/工程編號:	J3416/400.4/D0002	5		

#### Location Information 位置資料

Location 地點:	<b>Central Police St</b>	Station Compound. Nearby Utility Post No. 就近公用設施編號:	
Location Types 地點類 Address : (multiple answers allow 可選多於一項)		<ul> <li>□ Roadside 路旁</li> <li>□ X Open space 空地</li> <li>□ Exhibition Centre 展覽中心</li> <li>□ View Point 觀景台</li> <li>□ Walking / nature trail 行山徑 / 自</li> <li>□ Others (please specify)其他 (請說)</li> </ul>	

#### General Tree Information 基本樹木資料

<b>General Tree Information</b>	n 基本樹木資料			* Delete as a	appropriate 請把不合適的刪除
Main tree species in the group or minority tree species of significant size 在群組內的主要樹種或樹幹 胸徑或高度或樹冠範圍較大 的樹種 (Note 2)	Approx. number of trees in the relevant species or as a % of tree group 該樹種在群組內 的百份比/數目*	Range of tree height (m) 該樹種高度範圍	Overall health condition 整體健康狀況 (good, fair, poor 好,良,差)	Overall structural condition 整體結構狀況 (good, fair, poor 好,良, 差)	Other remarks (Any special tree condition, e.g. dying/dead, pest/disease problem and structural defects; and soil condition 其他評語 (樹木狀况例如: 凋謝/枯樹/病蟲害 或結構問題; 及泥土狀况)
Mangifera indica 芒果	17%, 1 No.	16M	FAIR	FAIR	To keep monitoring on the pest disease on the tree.
Aleurites moluccana 石栗	32% 2 Nos.	10-13M	FAIR	FAIR	No further action is required
Plumeria rubra 紅雞蛋花	17% 1 No.	7M	FAIR	FAIR	No further action is required
Araucaria cunninghamia 花旗杉	17% 1 No.	13M	FAIR	FAIR	No further action is required
Dracaena marginata 馬尾鐵	17% 1 No.	8M	FAIR	FAIR	To keep monitoring on the growth of the tree.

#### Target 目標

TARGET (people or property potentially affected by tree/branch failure) 目標 (因樹木倒塌或枝條斷裂而受影響的人或財產)	
Does target exist? 目標是否存在? x Yes 是 No 否	
Can target be moved?能否移除目標?	_
Can the use of site be restricted? 可否限制場地的使用? x Yes 是 No 否	
Frequency of use of location 使用該地點的頻密程度:	_
│ □ Occasional use 偶爾使用 □ Intermittent use 間歇使用 🔽 Frequent use 經常使用 🗌 Constant use 恆常使用	

#### Identification of Trees for Remedial Action or Detailed Tree Risk Assessment

識別下述樹木,以便採取風險緩減措施或進行詳細樹木風險評估

	ing under the following criteria 以下任何一項或多於一項類別	Number of trees 樹木數量	Remedial action or detailed tree risk assessment 緩減措施或進行詳細樹木風險評估
(1)	Trees on complaint list with structural or health problems 投訴個案中,結構或健康問題的樹木 (Note 1)	NII	
(2)	Mature trees belonging to species with brittle wood structure and having unsatisfactory health or structural conditions with failure potential 屬木質脆弱品種並已達成熟期及有倒塌風險的樹木 (Note 1)	NII	
(3)	Tree with major defects or health problems 有明顯缺陷或健康問題的樹木 (Note 1)	NII	
(4)	Trees growing in very stressful site conditions with failure potential 生長於非常擠壓環境而有倒塌風險的樹木 (Note 1)	NII	



$\cap$	an And	A REAL PROPERTY AND A REAL
Signature of Tree Inspection Officer : Signature of Endorsement Officer:		
Name of Contractor	Yan Wing (HK) Environment Management Ltd.	_ ~
Date:	29-2-2016	

- Note 1:
   If remedial action (such as pruning) undertaken cannot mitigate the potential risk of tree or branch failure, detailed tree risk assessment (using Form 2) should be carried out.

   備註 1:
   若風險緩減措施(如枝幹修剪)仍未能解決倒塌或枝條斷裂的潛在風險,應爲該樹進行詳細的樹木風險評估(表格 2)。
- Mmar. 1・ 石風破液液病用加吸加化料1993/DJ不能時代出場現代深層後的省社風液、認為次恆進口計和的均衡不風險計冶(表格 2)。 Note 2: Please read in conjunction with TMO's Guidelines on Tree Risk Assessment and Management Arrangement (Para 4.3, refers.)
- 備註 2: 請參閱樹木管理辨事處的樹木風險評估安排及管理指引(第 4.3 節)

I. TREE NUMBER: Tree-5 Mangifera indica 芒果

#### II. BASIC INFORMATION :

Height (m)	16m	Crown spread (m)	18m
DBH (mm)	1000mm	Overall Health Condition	Fair
		Good/Fair/Poor	
Date of Inspection	3 <sup>rd</sup> February 2016	Last Inspection Date	6 <sup>th</sup> January 2016

#### III. COMMENTS :

- 1. Overall health condition of the tree is fair.
- 2. Renovation work is in progress near the tree.
- 3. The planter is being re-built.
- 4. Signs of Pest (Mealy Bugs 粉狀介殼蟲) have apparently reduced due to pest control operation on 3<sup>rd</sup> July 2015.
- 5. Construction works are in progress outside the cordon zone.

#### IV. RECOMMENDATIONS :

1. To keep monitoring on the pest disease on the tree.


#### V. PHOTO RECORD :












ſ




Fig. 5 Health condition of the upper trunk also is fair.






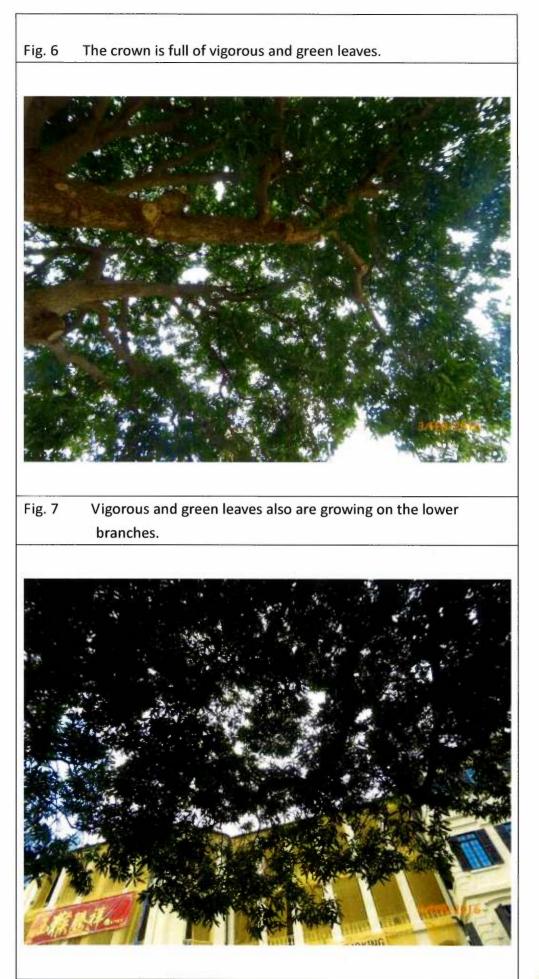




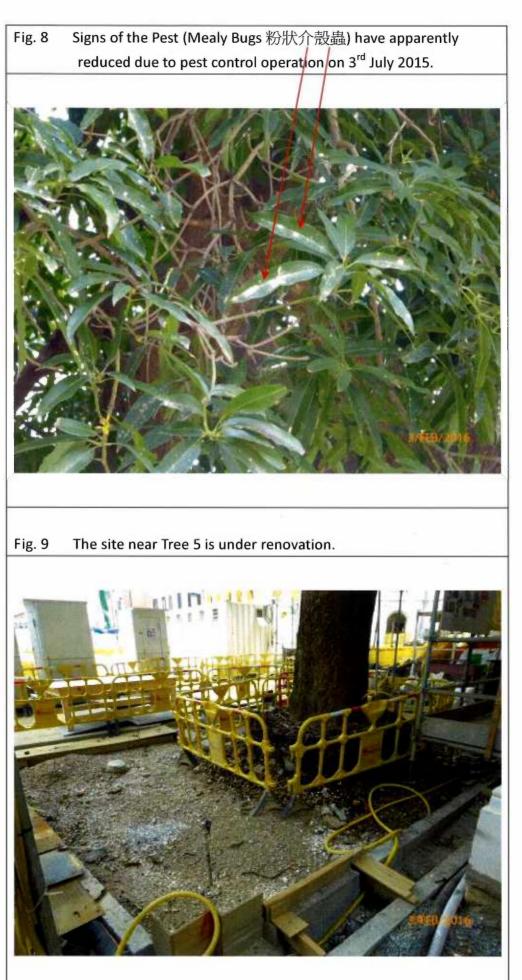



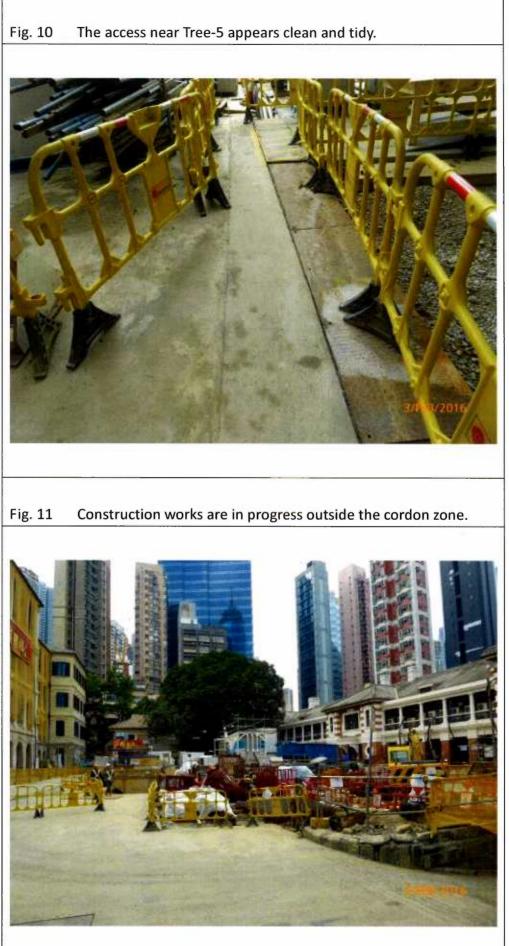



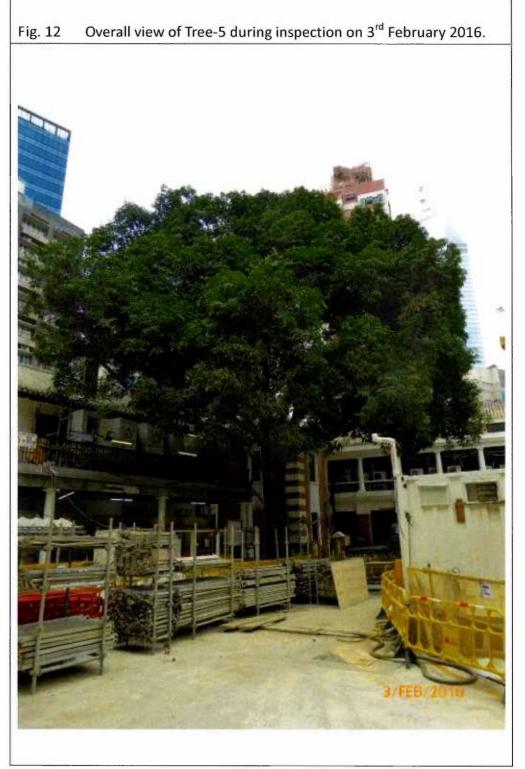

Signature of Inspection Officer : (Mr. LAU Man-chung, ISA CA-HK0050A) Signature of Endorsement Officer : (Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Yan Wing (HK) Environment Management Ltd.



29<sup>th</sup> February 2016 7

I. TREEE NUMBER: Tree-6 Aleurites moluccana 石栗

#### II. BASIC INFORMATION :

Height (m)	10m	Crown spread (m)	10m
DBH (mm)	510mm	Overall Health Condition	Fair
Data of loop action	ard Falance 2010	Good/Fair/Poor	cth
Date of Inspection	3 <sup>rd</sup> February 2016	Last Inspection Date	6 <sup>th</sup> January 2016

#### III. COMMENTS :


- 1. Overall health condition of the tree is fair.
- 2. Root collar is normal. The planter is covered with mulch and leaves.
- 3. The crown is full of vigorous and green leaves.
- 4. The site near the tree is clean and tidy.
- 5. Construction works are in progress near the tree.

#### IV. RECOMMENDATIONS :


- 1. No further action is required.
- V. PHOTO RECORD :






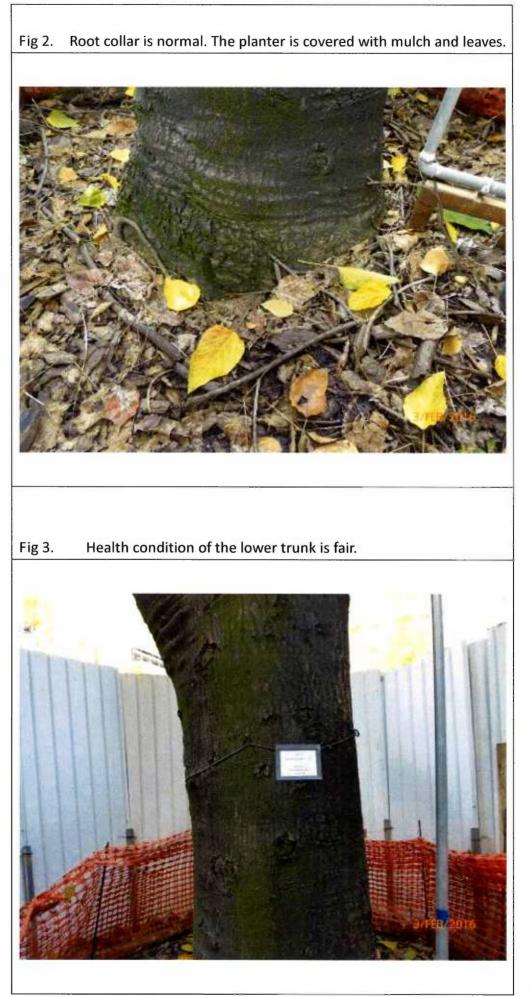



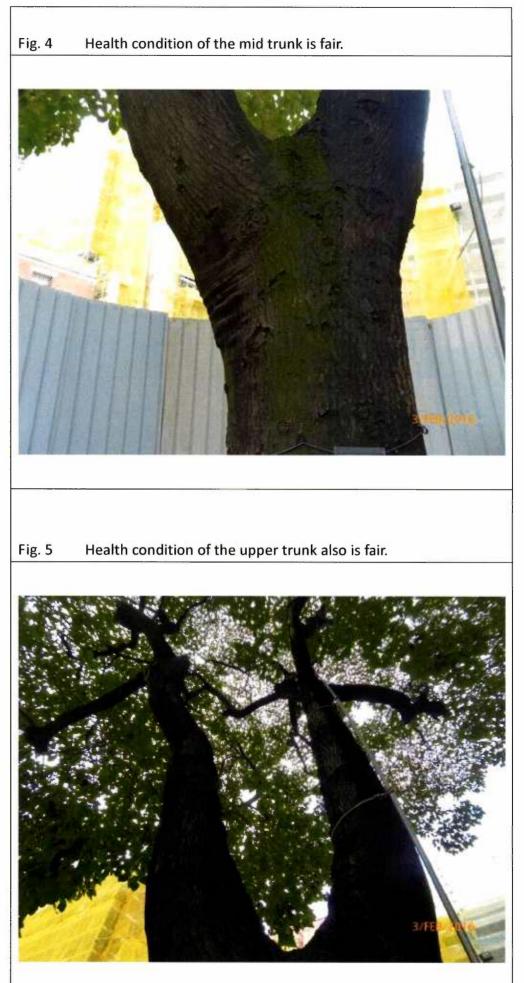



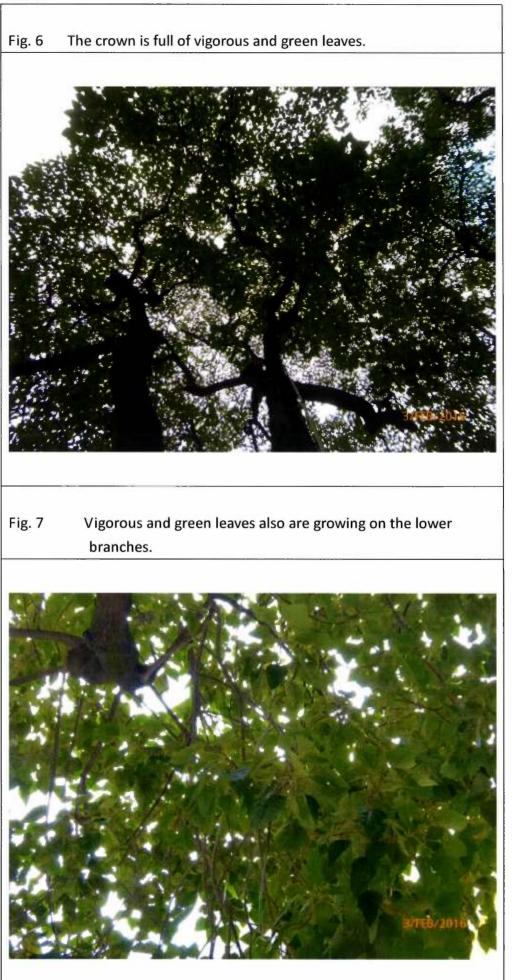












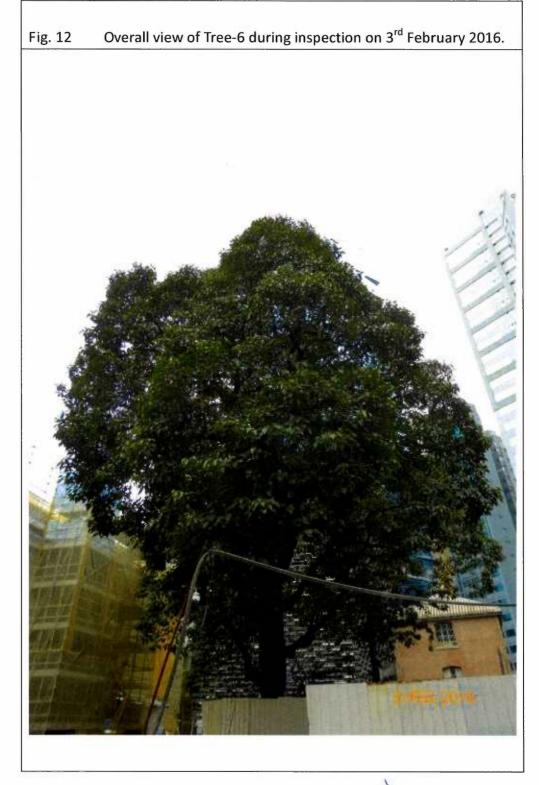

Signature of Inspection Officer : (Mr. LAU Man-chung, ISA CA–HK0050A) Signature of Endorsement Officer : (Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Yan Wing (HK) Environment Management (td. 29th February 2016



#### I. TREEE NUMBER: Tree-7 Aleurites moluccana 石栗

#### II. BASIC INFORMATION :

Height (m)	13m	Crown spread (m)	12m
DBH (mm)	650mm	Overall Health Condition Good/Fair/Poor	Fair
Date of Inspection	3 <sup>rd</sup> February 2016	Last Inspection Date	6 <sup>th</sup> January 2016

#### III. COMMENTS :

- 1. Overall health condition of the tree is fair.
- 2. Root collar is normal. The planter is covered with mulch and leaves.
- 3. The crown is full of vigorous and green leaves.
- 4. The access near Tree-7 is clean and tidy.
- 5. Some construction tools are placed near the tree.


#### IV. RECOMMENDATIONS :

1. No further action is required.

#### V. PHOTO RECORD :






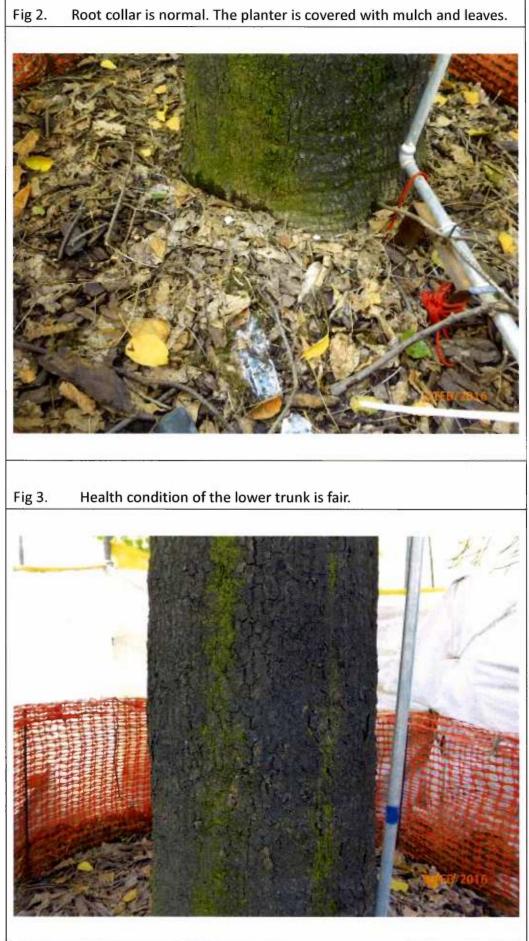







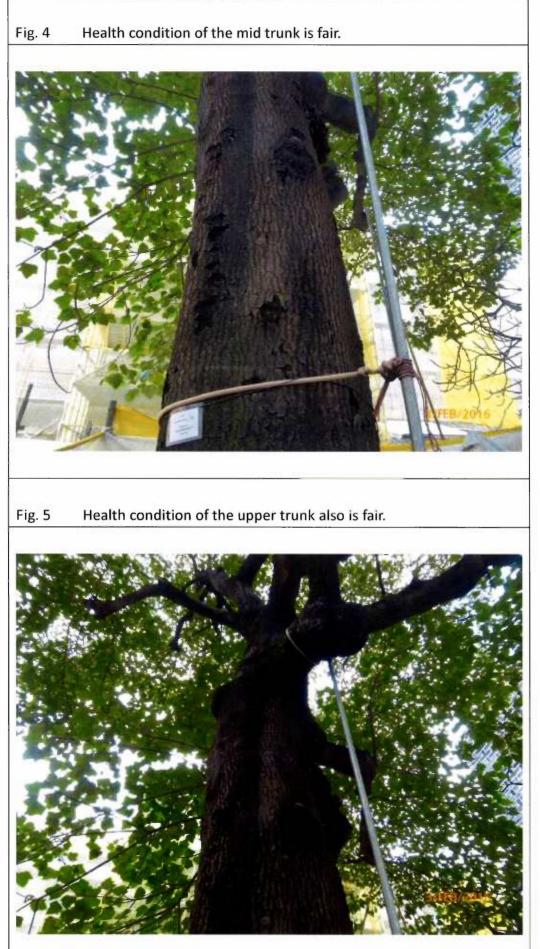




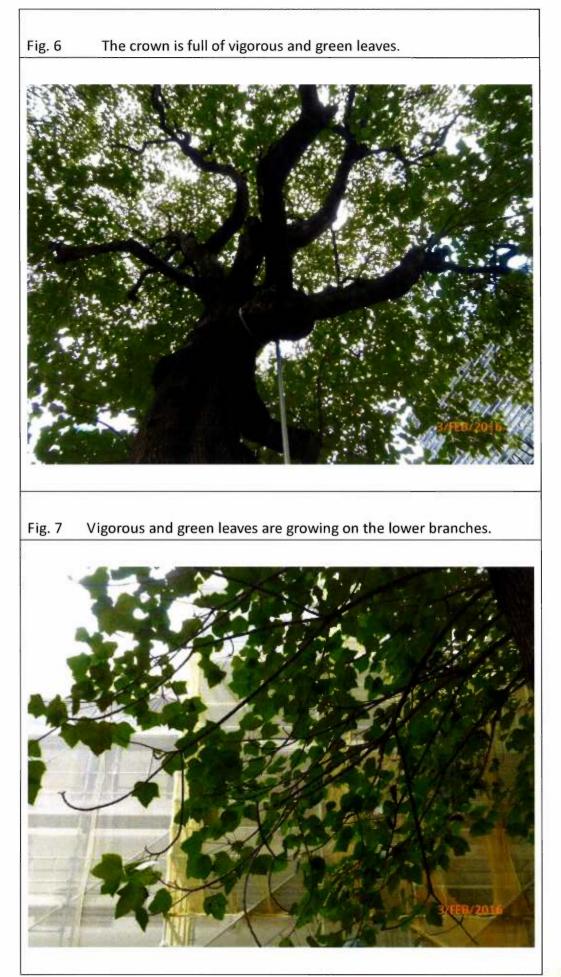




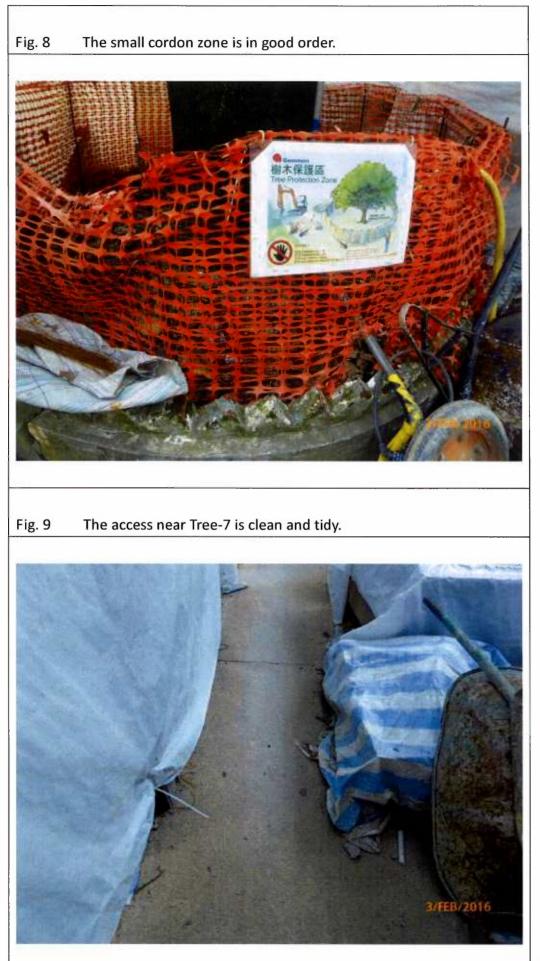



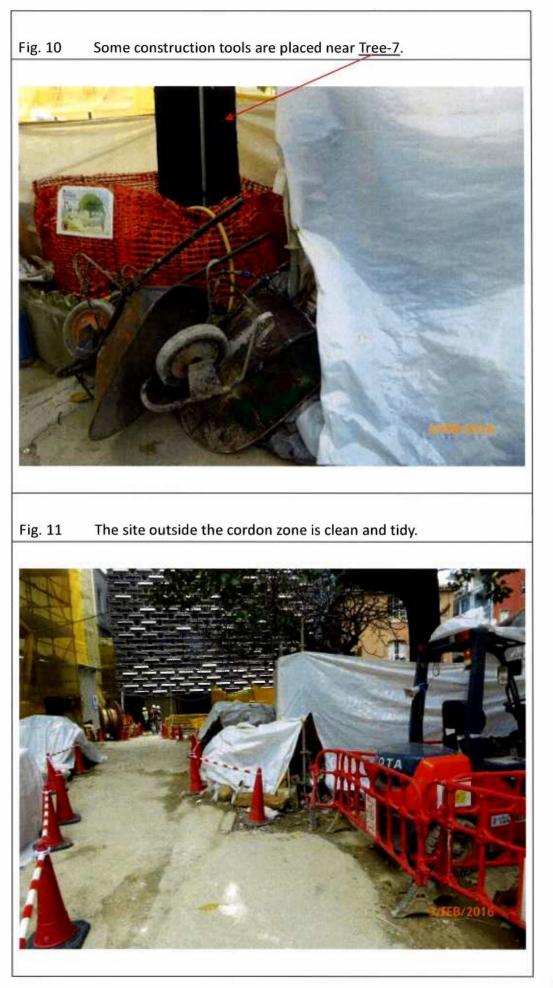



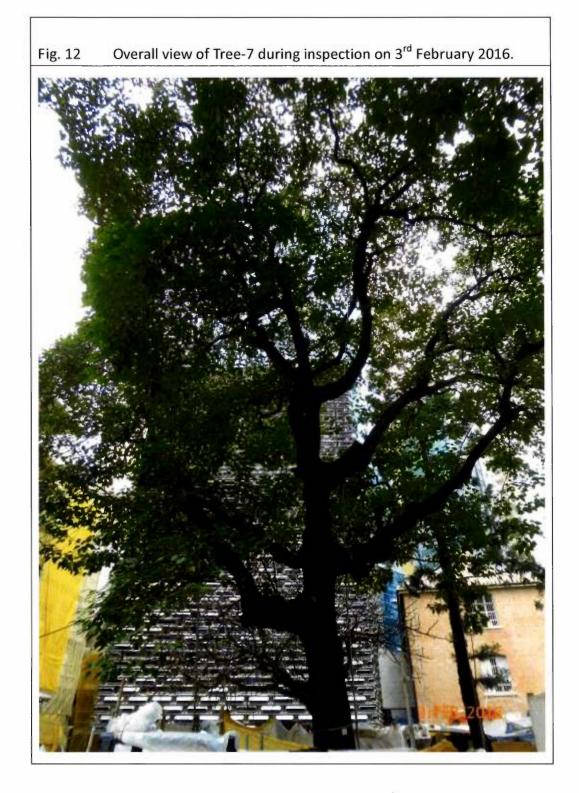

Signature of Inspection Officer : (Mr. Lau Man-chung, ISA CA–HK0045A) Signature of Endorsement Officer : (Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Yan Wing (HK) Environment Management Ltd. 29th February 2016



#### 1. TREEE NUMBER: Tree-8 Plumeria rubra 紅雞蛋花

#### II. BASIC INFORMATION :

Height (m)	7m	Crown spread (m)	9m
DBH (mm)	430mm	Overall Health Condition Good/Fair/Poor	Fair
Date of Inspection	3 <sup>rd</sup> February 2016	Last Inspection Date	6 <sup>th</sup> January 2016

#### III. COMMENTS :

- 1. Overall health condition of the tree is fair.
- 2. Root collar is normal. The planter is covered with mulch and leaves.
- 3. Leaves on the crown are sparse.
- 4. The access near Tree-8 is clean and tidy.
- 5. Construction works are in progress outside the cordon zone.


#### IV. RECOMMENDATIONS :

1. No further action is required.


#### 1. PHOTO RECORD :






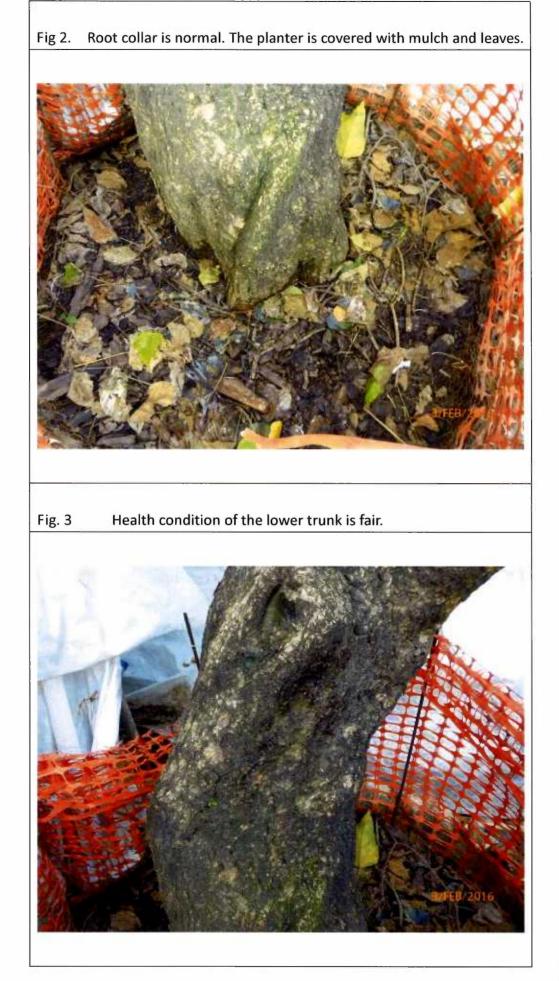




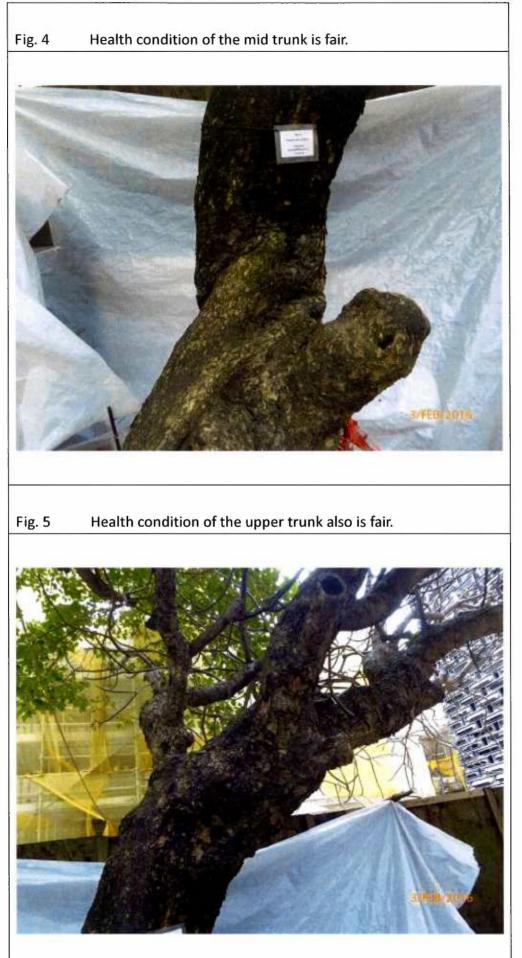





.

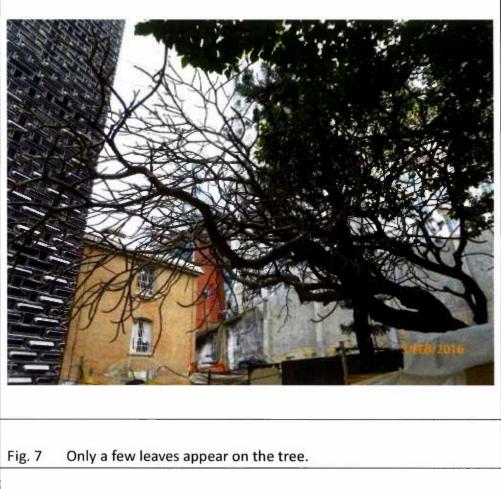







#### Fig. 8 The small cordon zone is in order.





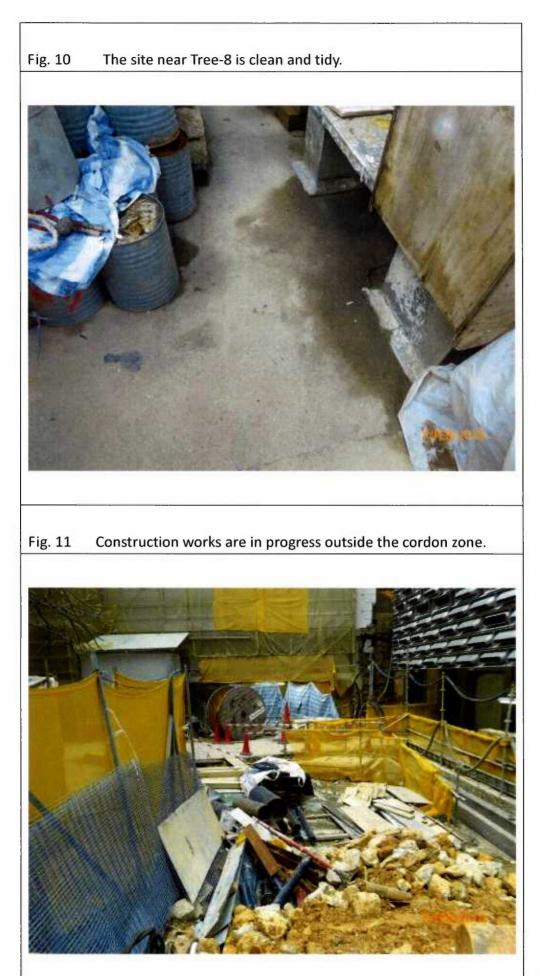



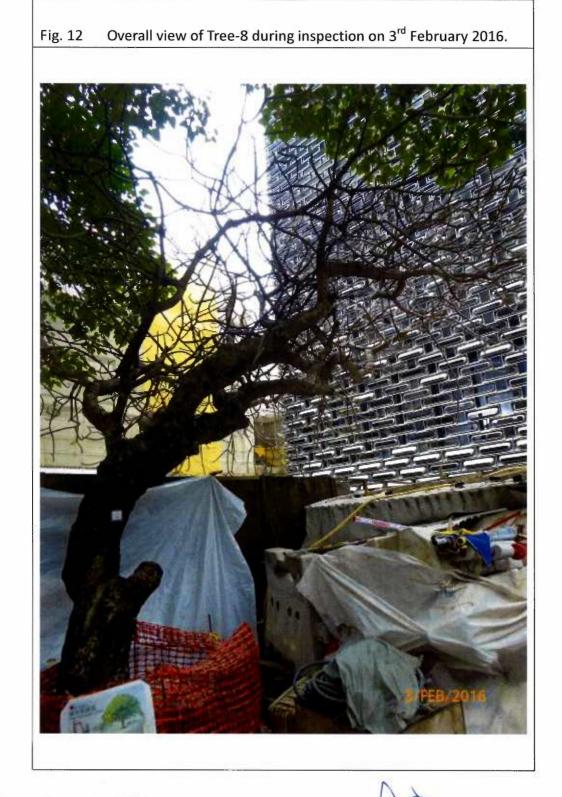

Signature of Inspection Officer : (Mr. LAU Man-chung, ISA CA–HK0050A) Signature of Endorsement Officer : (Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Yan Wing (HK) Environment Management Utd.



29<sup>th</sup> February 2016

#### I. TREEE NUMBER: Tree - 9 Araucaria cunninghamia 花旗杉

#### II. BASIC INFORMATION :

Height (m)	13m	Crown spread (m)	5m
DBH (mm)	230mm	Overall Health Condition	Fair
		Good/Fair/Poor	
Date of Inspection	3 <sup>rd</sup> February 2016	Last Inspection Date	6 <sup>th</sup> January 2016

#### III. COMMENTS :

- 1. Overall health condition of the tree is fair.
- 2. Root collar is normal. The planter is covered with mulch and leaves.
- 3. Green and vigorous leaves appear on the tree.
- 4. The site near the tree is clean and tidy.
- 5. Construction works are in progress outside the cordon zone.

#### IV. RECOMMENDATIONS :

1. No further action is required.


#### V. PHOTO RECORD :











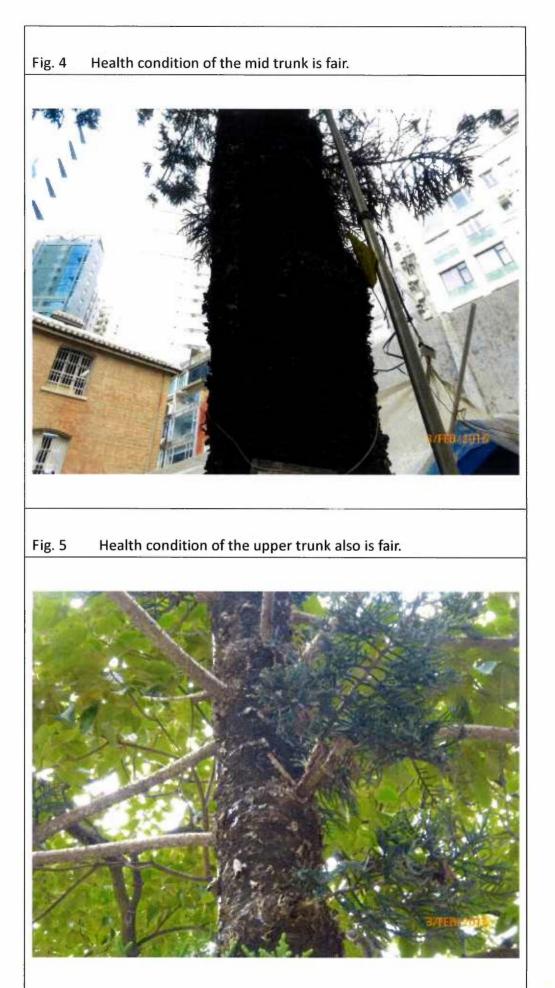




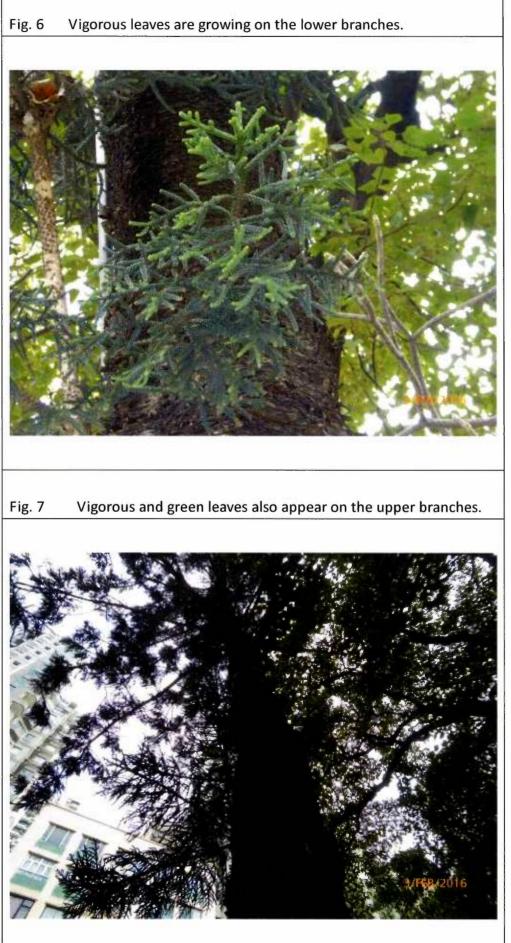




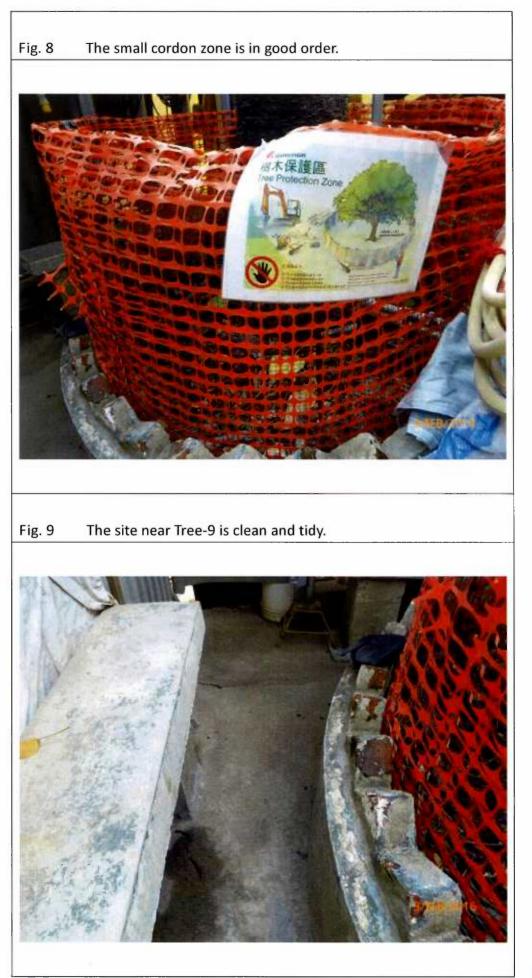



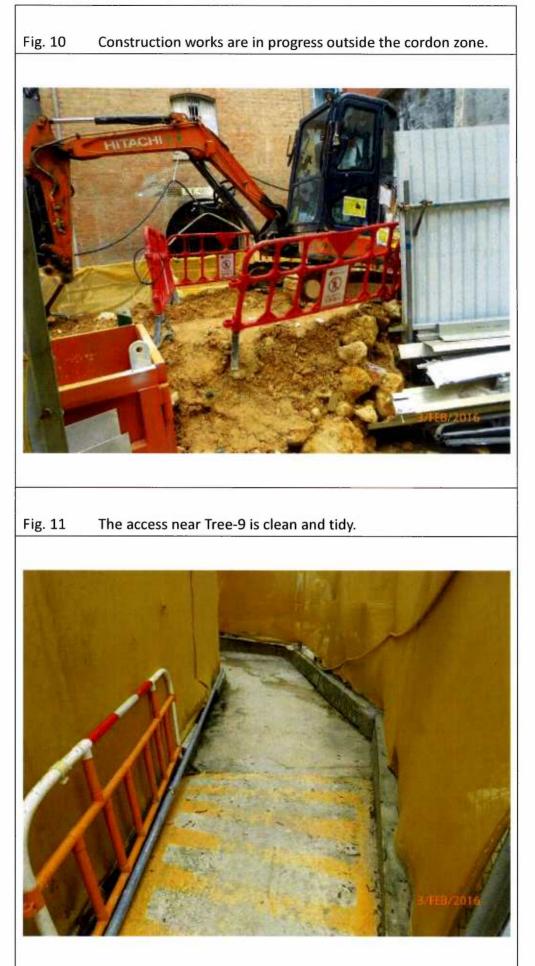



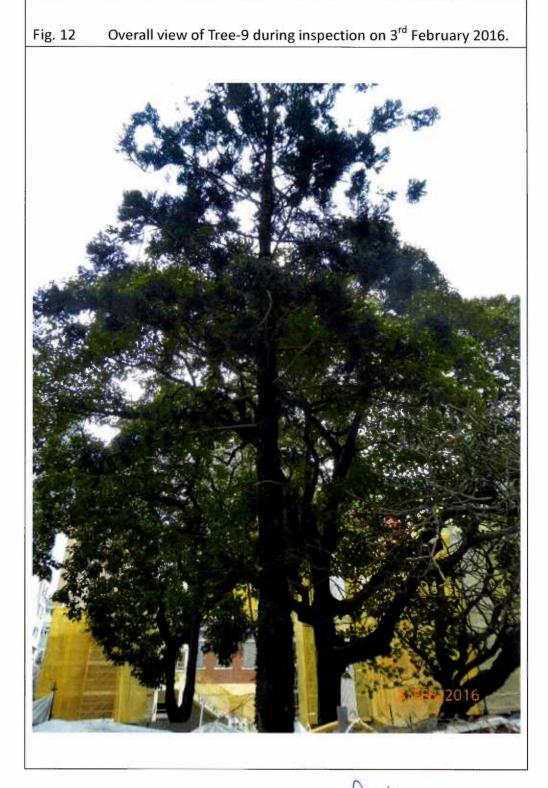

Signature of Inspection Officer : (Mr. LAU Man-chung, ISA CA–HK0050A) Signature of Endorsement Officer : (Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Dated this :

Yan Wing (HK) Environment Management Ltd).



29<sup>th</sup> February 2016 7

## Inspection Report for the 6 Existing Trees <u>at Central Police Station Compound</u> ( Contract Ref. : J3416/400.4/D00025 )

#### I. TREEE NUMBER: Tree -11 Dracaena marginata 馬尾鐵

#### II. BASIC INFORMATION :

Height (m)	8m	Crown spread (m)	2m
DBH (mm)	170mm	Overall Health Condition Good/Fair/Poor	Fair
Date of Inspection	3 <sup>rd</sup> February 2016	Last Inspection Date	6 <sup>th</sup> January 2016

#### III. COMMENTS :

- 1. Health condition of the tree is getting better.
- 2. Young and green leaves are growing on the root collar of the tree.
- 3. Withered leaves have apparently reduces on the tree.
- 4. Construction works are in progress near the tree.


#### IV. RECOMMENDATIONS :

1. To keep monitoring on the growth of the tree.


### V. PHOTO RECORD :






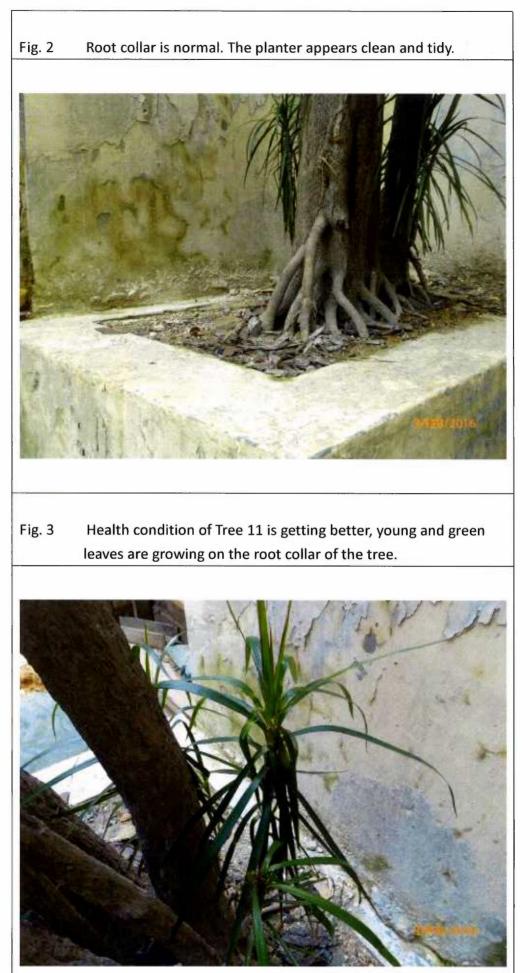







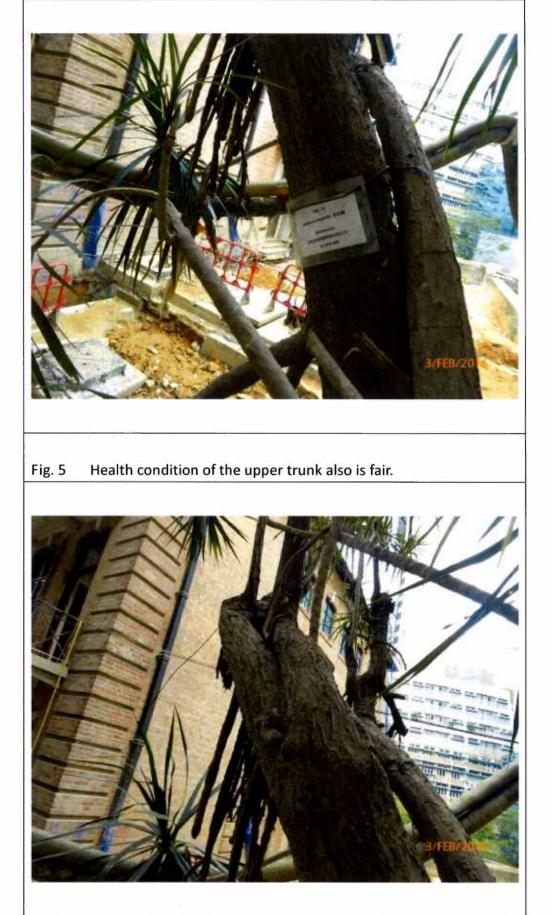



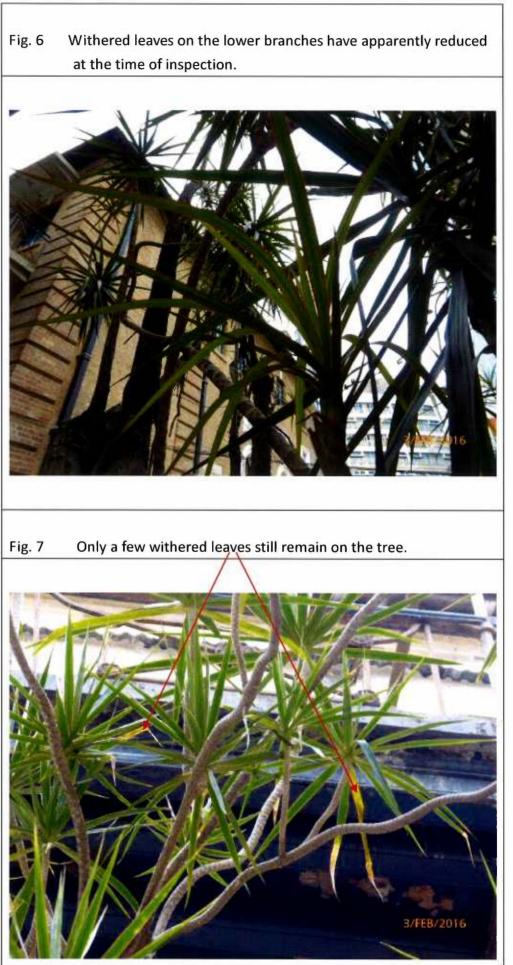




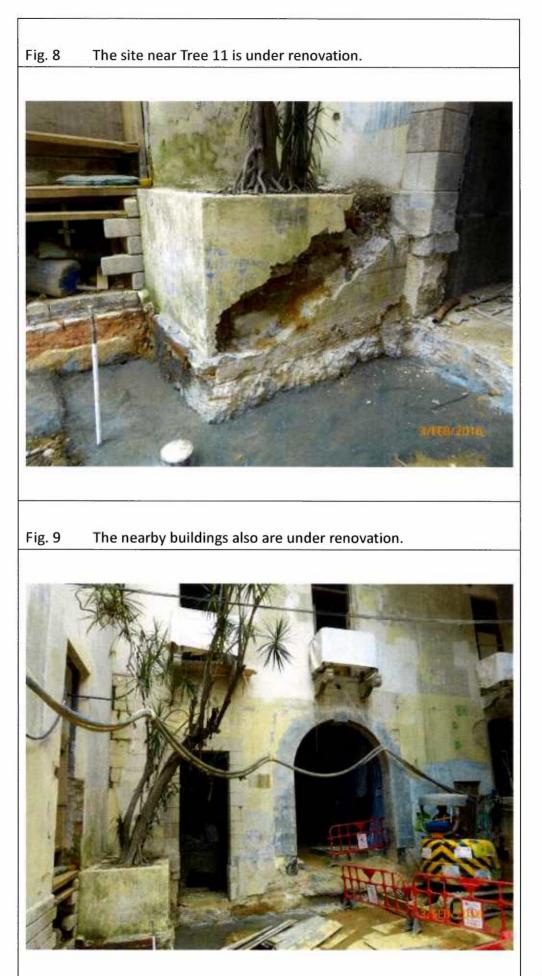


.



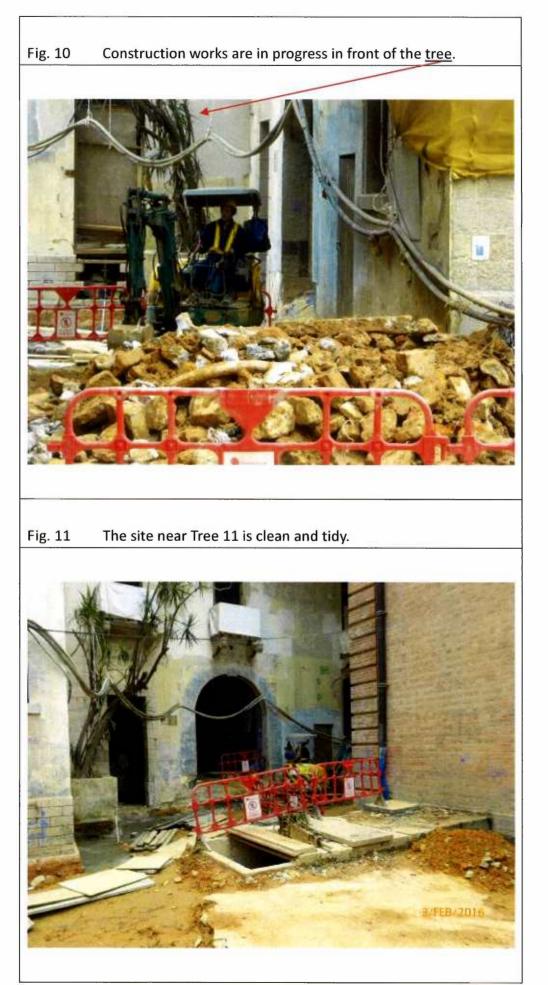



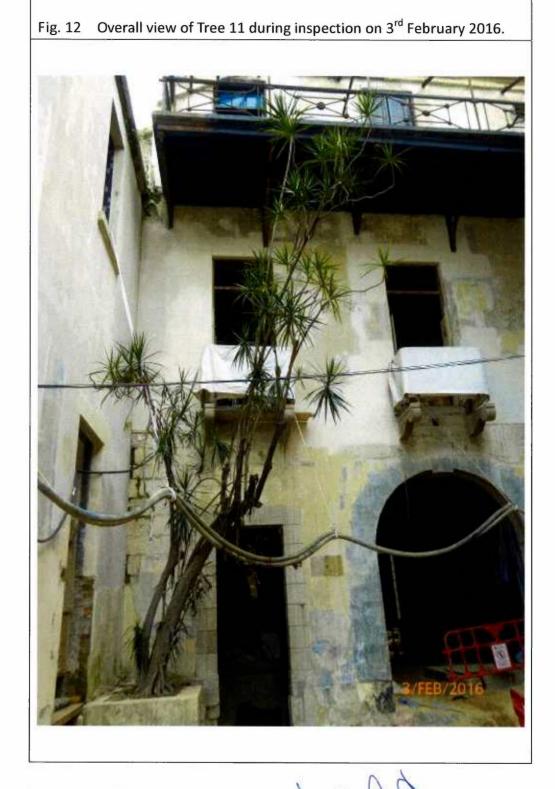

Signature of Inspection Officer : (Mr. LAU Man-chung, ISA CA–HK0050A) Signature of Endorsement Officer : (Mr. WONG Pak-hay, Contract Manager)

Name of Contractor :

Dated this :

Yan Wing (HK) Environment Management Ltd.



29<sup>th</sup> February 2016

Annex K

Environmental Complaint, Environmental Summons and Prosecution Log

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	4	0
April 2012	0	0
May 2012	0	0
June 2012	2	0
July 2012	1	0
August 2012	0	0
September 2012	0	0
October 2012	0	0
November 2012	2	0
December 2012	0	0
January 2013	0	0
February 2013	1	0
March 2013	1	0
April 2013	0	0

Annex K Cumulative Complaint and Summons/Prosecutions Log

ENVIRONMENTAL RESOURCES MANAGEMENT


Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
May 2013	0	0
June 2013	0	0
July 2013	0	0
August 2013	0	0
September 2013	0	0
October 2013	0	0
November 2013	0	0
December 2013	0	0
January 2014	2	0
February 2014	1	0
March 2014	1	0
April 2014	1	0
May 2014	0	0
June 2014	0	0
July 2014	2	0
August 2014	3	0
September 2014	2	0
October 2014	1	0
November 2014	0	0

<b>Reporting Month</b>	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2014	0	0
January 2015	0	0
February 2015	1	0
March 2015	1	0
April 2015	0	0
May 2015	1	0
June 2015	1	0
July 2015	1	0
August 2015	1	0
September 2015	0	0
October 2015	0	0
November 2015	0	0
December 2015	0	0
January 2016	0	0
February 2016	0	0
Overall Total	30	0

#### ENVIRONMENTAL RESOURCES MANAGEMENT

Annex L

Records of Vibration Monitoring for Piling works

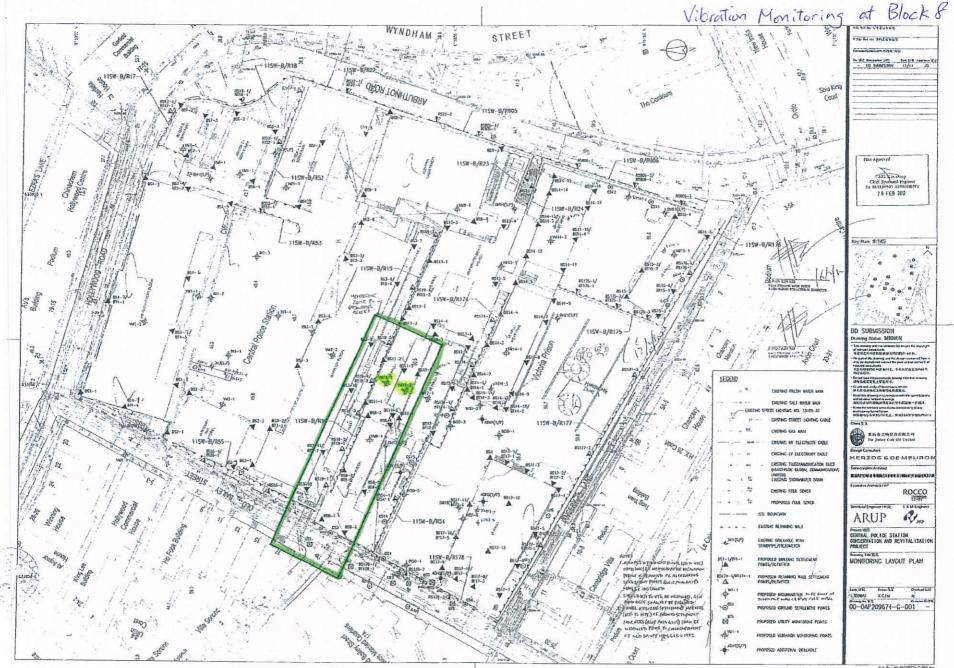

Cut fie 1 10-00129571-G-001#-0

						(Block 8 F	oundation)	
WWW 恆誠建築工程有限公司 Win Win Way Construction Company Ltd.		Monitoring	Check Pts.	Trigger Levels				
				Alert level	Alarm level	Action level		
			Vibrating M #Vibration at 1		2mm/s	2.5mm/s	3mm/s	
		#vibration at I highest Stru		5.0mm/s	6.0mm/s	7.5mm/s		
			Vibrati	on Record				
Project Title: Central Po	olice Station Co	onservation & R	evitalization	Project No: W	P201	1-Feb-2016	to to	29-Feb-20
POINT	VM11-1#	VM11-2						
		,						
DATE PD/(m)	mm/s	mm/s					+ +	
19-Jun-2012 (Initial)	0.13	0.19						
1-Feb-2016	0.109	0.101						
2-Feb-2016	0.105	0.103						
3-Feb-2016	0.102	0.109						
4-Feb-2016	0.103	0.106						
5-Feb-2016	0.094	0.105						
6-Feb-2016	0.087	0.100						
7-Feb-2016				Sunday				
8-Feb-2016				Holiday				
9-Feb-2016				Holiday				
10-Feb-2016	0.075			Holiday	7		1 1	
11-Feb-2016	0.052	0.070						
12-Feb-2016 13-Feb-2016	0.059 0.067	0.061 0.082						
13-Feb-2016	0.007	0.082		Sunday			1	
15-Feb-2016	0.098	0.103		Sunday				
16-Feb-2016	0.100	0.108						
17-Feb-2016	0.105	0.107						
18-Feb-2016	0.101	0.106					1	
19-Feb-2016	0.103	0.105						
20-Feb-2016	0.107	0.109						
21-Feb-2016				Sunday				
22-Feb-2016	0.105	0.100						
23-Feb-2016	0.103	0.107						
24-Feb-2016	0.101	0.105						
25-Feb-2016	0.106	0.114						
26-Feb-2016	0.097	0.101						
27-Feb-2016	0.102	0.106						
28-Feb-2016	0.477			Sunday			1 1	
29-Feb-2016	0.105	0.102						

Annex M

Records of Vibration Monitoring for Other Construction Works

Structural Additions and



ien India	erations at 13	BD. Rel No. 原字型な楽編編 BD. Rel No. 原字型な楽編編
	815700	22-3/3066/10/BLK11(HU) (S) F.S.D. Ref No 纳防原植築編號
1991	12 80	Revision/Submission 性较粒/极批
17		No.编號 Description 說明 Date 日界 Approved事
	Star and	- BD_SUBMISSION (50) 12/11 JS A BD_SUBMISSION (01) 03/12 JS
11	a,	B BC SUBMISSION (17) 03/12 JS C BD SUBMISSION RW BATCH 1 03/12 JS
110	Shiu King	D FOR INFROMATION (50) 03/12 JS E BO SUBMISSION (51) 05/12 JS
111	Cont	F BD SUBMISSION (04) 05/12 JS
A.	100	H BD SUBMISSION (14) 05/12 JS
f. g	A	J BD SUBMISSION RW BATCH 2 D6/12 JS K BD SUBMISSION (06&07) 07/12 JS
		L BD SUBMISSION (01)(HQ)07/12 JS M BD SUBMISSION (11) 07/12 JS
1	The second second	
Anthe Ad	10 PX	
	The Marine The	
1	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	
530-61	and the second	Plan Approved
11-		CHIONG Kam-yueng Jacky
	Jun.	Chief Structural Engineer for BUILDING AUTHORITY
12	811	- 3 OCT 2012
19	Ce.	
11SW-B/	/R176	Key Plan 索引圖 N
	E	6 9 9 Y
$\sim$	000	• • • • ///
	-	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0
	. /	0 0
~~ /	Ke/	e
a	AP .	
1.7.19	[]	BD SUBMISSION
115	M	Drawing Status 裂麗狀況 - This drawing and the contents berein are the copyright
19	WAN KIN KIN Teat Fismate MICE FHKIE HEOISTERED STRUCTURAL SHAINEER	of relevant consultants. 本藏紙及其內容的版樹屬有關觀回公司所有。 - No part of the drawing and the design contained herein
1	\$ v.	may be reproduced without the prior written consent of relevant consultants. 未經有關關問公司書面同意。不可接對此服師內任何
		- Do not take measurements directly from this crawing.
100	EXISTING FRESH WATER MAIN	初勿直浪從屬紙上量度尺寸。 Check and vortily all dimensions on site 研有尺寸必须在工业现场找费及客栈。
	EXISTING SALT WATER MAIN	<ul> <li>Read this drawing in conjunction with the specifications and all other related drawings, 此躍紙必須與契格說明實及其它容顯圓紙一併閱講。</li> </ul>
	COMPACTION AND A STATE OF A STATE	<ul> <li>Notify the relevant consultants immediately of any discrepancy found tieren, 如容現內容有任何樣級之處。應立創通知有範疇問公司。</li> </ul>
EXISTING ST	REET LIGHTING NC. 33488-A1	
EXISTING ST	REET LIGHTING NC. 33488-A1 EXISTING STREET LIGHTING CABLE	and the second
-11		如發現內容有任何勝級之處。應立歸通知有與朝間公司。 Client 要走 委告令文物保育有限公司
	EXISTING STREET LIGHTING CABLE	Client 聚主
- 11	EXISTING STREET LIGHTING CABLE	Client 憲主 算馬 余文协促 自有职 合词 The , seker Club CP Limited Design Consultant
	EXISTING STREET LIGHTING CABLE EXISTING GAS MAIN EXISTING HV ELECTRICITY CABLE EXISTING LV ELECTRICITY CABLE EXISTING TELECOMVUMICATION DUCT	Client 憲主 算馬 余文协促 自有职 合词 The , seker Club CP Limited Design Consultant
	EXISTING STREET LIGHTING CABLE EXISTING CAS WAIN EXISTING HV ELECTRICITY CABLE EXISTING TU ELECTRICITY CABLE EXISTING TELECOMMUNICATION DUCT (HUTCHNSON GLOBAL COMMUNICATIONS LUMITED)	Cifent 推击
- 11 250 13224 13224	EXISTING STREET LIGHTING CABLE EXISTING CAS MAIN EXISTING HV ELECTRICITY CABLE EXISTING TU ELECTRICITY CABLE EXISTING TELECOMVUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED) EXISTING STORYMATER DRAIN	Client 兼主
- 11	EXISTING STREET LIGHTING CABLE EXISTING GAS MAIN EXISTING HV ELECTRIGITY CABLE EXISTING TV ELECTRICITY CABLE EXISTING TELECOMVUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED) EXISTING STORWATER DRAIN EXISTING FOLL SEVER	Cifert 推击 算具有文协保育有架合词 Thr , extent Club CP 1 raited Design Consultant H E R Z O G & D E M E U R D M Conservation Architest HGR(KG3 HTML X75 HGR(KB F F F F F F F F F F F F F F F F F F F
- 11	EXISTING STREET LIGHTING CABLE EXISTING CAS MAIN EXISTING FAY ELECTRICITY CABLE EXISTING TU ELECTRICITY CABLE EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED) EXISTING STORWAATER DRAIN EXISTING FOUL SEWER PROPOSED FOUL SEWER	Ciferet 兼主
- 11	EXISTING STREET LIGHTING CABLE EXISTING CAS WAIN EXISTING CAS WAIN EXISTING THE ELECTRICITY CABLE EXISTING TELECOMMUNICATION DUCT (HUTCHSON GLOBAL COMMUNICATIONS LUNITED) EXISTING STORNMATER DRAIN EXISTING FOUL SEVER PROPOSED FOUL SEVER BOUNDARY	Client 兼主
- 11	EXISTING STREET LIGHTING CABLE EXISTING CAS MAIN EXISTING FAY ELECTRICITY CABLE EXISTING TU ELECTRICITY CABLE EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED) EXISTING STORWAATER DRAIN EXISTING FOUL SEWER PROPOSED FOUL SEWER	Ciferet 兼主 新品作文协保育有职会司 Ter, etch Club IP Limited Design Consultant H E R Z D G & D E M E U R D N Conservation Archites: HR91009 # HEATE HAR STATE HOLD Executive Archites! R80000 # HEATE HAR STATE HOLD Executive Archites! R80000 # HEATE HAR STATE HOLD Executive Archites! R80000 # HEATE HAR STATE HOLD From Structural Engineer / RSE R & M Engineer A R U P Project 均自
- 11	EXISTING STREET LIGHTING CABLE EXISTING CAS WAIN EXISTING CAS WAIN EXISTING THE ELECTRICITY CABLE EXISTING TELECOMMUNICATION DUCT (HUTCHSON GLOBAL COMMUNICATIONS LUNITED) EXISTING STORNMATER DRAIN EXISTING FOUL SEVER PROPOSED FOUL SEVER BOUNDARY	Client 兼主 新生命文物保育有职会司 Ter Jecker Club CP Linited Design Consultant H E R Z D G & D E M E U R D M Conservation Architect Resident Architect Executive Architect / AP Executive Architect / AP
- 11	EXISTING STREET LIGHTING CABLE EXISTING GAS MAIN EXISTING FAY ELECTRICITY CABLE EXISTING THE ELECTRICITY CABLE EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED) EXISTING FOUL SEWER PROPOSED FOUL SEWER BOUNDARY TING RETAINING WALL TING DRULHOLE WITH IDDPIPE/PREZOMETER PROFOSED BUILDING SETTLEMENT	Citient 兼主 新品作文协保育 打限公司 Te::::::::::::::::::::::::::::::::::::
- 11	DISTING STREET LIGHTING CABLE EXISTING CAS MAIN EXISTING FAV ELECTRICITY CABLE EXISTING TU ELECTRICITY CABLE EXISTING TELECOMMUNICATION DUCT (HUTCHISON CLOBAL COMMUNICATIONS LIMITED) EXISTING FOUL SEWER PROPOSED FOUL SEWER BOUNDARY TING RETAINING WALL TING DRILLHOLE WITH DOPIDE/PIEZOMETER POSED BULDING SETTLEMENT TS/TLITMETER	Client 独主 新馬 余 文 坊 保賀 打 税 分 动 The Jinchen Club CP Linested Design Consultant H E R Z D G & D E M E U R D N Conservation Architect RESIGNATION AND REVITALISATION Project 福音 CONSERVATION AND REVITALISATION PROJECT
- 11	EXISTING STREET LIGHTING CABLE EXISTING GAS MAIN EXISTING FAY ELECTRICITY CABLE EXISTING THE ELECTRICITY CABLE EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED) EXISTING FOUL SEWER PROPOSED FOUL SEWER BOUNDARY TING RETAINING WALL TING DRULHOLE WITH IDDPIPE/PREZOMETER PROFOSED BUILDING SETTLEMENT	Citient 兼主 新品作文协保育 打限公司 Te::::::::::::::::::::::::::::::::::::
- 11	EXISTING STREET LIGHTING CABLE EXISTING CAS MAIN EXISTING CAS MAIN EXISTING FUR ELECTRICITY CABLE EXISTING TELECOMULUNCATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LUNITED) EXISTING STORWAATER DRAIN EXISTING FOUL SEWER PROPOSED FOUL SEWER BOUNDARY TING RETAINING WALL TING DRILLHOLE WITH IDIPIE/PREZOMETER POSED BULDING SETTLEMENT TS/TILTMETER POSED FAINING WALL SETTLEMENT TS/TILTMETER	Citient 兼主 新品作文协保育 打限公司 Te::::::::::::::::::::::::::::::::::::
- 11	DISTING STREET LIGHTING CABLE EXISTING CAS WAIN EXISTING CAS WAIN EXISTING FUE ELECTRICITY CABLE EXISTING TELECOMULVICATION DUCT (NUTCHISON GLOBAL COMMUNICATIONS LIMITED) EXISTING FOLL SEWER PROPOSED FOUL SEWER BOUNDARY TING RETAINING WALL TING DRILLHOLE WITH HOPIPE/PIEZOMETER POSED BUILDING SETTLEMENT TS/TILTMETER POSED RETAINING WALL SETTLEMENT TS/TILTMETER	Client 兼主 新品 命文 物 保育 有 脱 合 动 Ter, etch Club CP Liested Design Consultant H E R Z D G & D E M E U R D N Conservation Archites: Registred a maximum state a conservation Conservation Archites: Registred a maximum state a conservation (1) (1) (1) (1) (1) (1) (1) (1) (1) (1)
- 11	EDISTING STREET LIGHTING CABLE EXISTING CAS MAIN EXISTING FAV ELECTRICITY CAGLE EXISTING THE LECORVILINGATION DUCT (HUTCHSON GLOBAL COMMUNICATIONS LIMITED) EXISTING STORWHATER DRAIN EXISTING FOUL SEWER PROPOSED FOUL SEWER BOUNDARY TING RETAINING WALL ENG DRILLHOLE WITH IDOPIE/FIEZOMETER POSED BULDING SETTLEMENT T3/TULTMETER POSED METAINING WALL SETTLEMENT T3/TULTMETER	Client 兼主 新生命 文 的 保育 有 积 合 而 Ter , exten Club CP Linsterd Design Consultant H E R Z D G & D E M E U H D N Concernation Architect RESOLUTIVE Architect RESOLUTIVE Architect / AP ROCCOO LIPPOP Structural Engineer / RSE E & M Engineer CENTRAL POLICE STATION CONSERVATION AND REVITAL ISATION PROJECT Drawing Tale 書名 MONITORING LAYOUT PLAN Scient EM Drawin 報酬 Concerled EM Concerled An Concerled An Concer
- 11	DISTING STREET LIGHTING CABLE EXISTING CAS WAIN EXISTING CAS WAIN EXISTING FUE LECTRICITY CABLE EXISTING TELECOMULVICATION DUCT (NUTCHISON GLOBAL COMMUNICATIONS LUNITED) EXISTING FOLL SEWER PROPOSED FOUL SEWER BOUNDARY TING RETAINING WALL TING DRILLHOLE WITH HOPIPE/PIEZOMETER POSED BUILDING SETTLEMENT TS/TILTMETER POSED RETAINING WALL SETTLEMENT TS/TILTMETER	Client 兼主 新品 命文 物 保育 有 脱 合 动 Ter, etch Club CP Liested Design Consultant H E R Z D G & D E M E U R D N Conservation Archites: Registred a maximum state a conservation Conservation Archites: Registred a maximum state a conservation (1) (1) (1) (1) (1) (1) (1) (1) (1) (1)
- 11	EDISTING STREET LIGHTING CABLE EXISTING CAS MAIN EXISTING FAV ELECTRICITY CAGLE EXISTING THE LECORVILINGATION DUCT (HUTCHSON GLOBAL COMMUNICATIONS LIMITED) EXISTING STORWHATER DRAIN EXISTING FOUL SEWER PROPOSED FOUL SEWER BOUNDARY TING RETAINING WALL ENG DRILLHOLE WITH IDOPIE/FIEZOMETER POSED BULDING SETTLEMENT T3/TULTMETER POSED METAINING WALL SETTLEMENT T3/TULTMETER	Client 兼主 新品 命文 物 保育 有 脱 合 动 Ter, etch Club CP Liested Design Consultant H E R Z D G & D E M E U R D N Conservation Archites: Registred a maximum state a conservation Conservation Archites: Registred a maximum state a conservation (1) (1) (1) (1) (1) (1) (1) (1) (1) (1)

# Vibration Monitoring Record (February)

	Block 11			
Point	VM11-1	VM11-2		
Date	mm/s	mm/s		
01-Feb-16	0.109	0.101		
02-Feb-16	0.105	0.103		
03-Feb-16	0.102	0.109		
04-Feb-16	0.103	0.106		
05-Feb-16	0.094	0.105		
06-Feb-16	0.087	0.100		
07-Feb-16	Sun	day		
08-Feb-16	Hol	iday		
09-Feb-16	Hol	iday		
10-Feb-16	Hol	iday		
11-Feb-16	0.052	0.070		
12-Feb-16	0.059	0.061		
13-Feb-16	0.067 0.082			
14-Feb-16	Sunday			
15-Feb-16	0.098	0.103		
16-Feb-16	0.100	0.108		
17-Feb-16	0.105	0.107		
18-Feb-16	0.101	0.106		
19-Feb-16	0.103	0.105		
20-Feb-16	0.107	0.109		
21-Feb-16	Sunday			
22-Feb-16	0.105	0.100		
23-Feb-16	0.103	0.107		
24-Feb-16	0.101	0.105		
25-Feb-16	0.106	0.114		
26-Feb-16	0.097	0.101		
27-Feb-16	0.102	0.106		
28-Feb-16	Sunday			
29-Feb-16	0.105	0.102		
