QUARTERLY EM&A REPORT

The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: 23rd Quarterly EM&A Report (1 May 2017 to 31 July 2017)

Issue Date: October 2017

Environmental Resources Management

16/F Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

QUARTERLY EM&A REPORT

The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: 23rd Quarterly EM&A Report (1 May 2017 to 31 July 2017)

Issue Date: October 2017

Reference 0095646

For and on behalf of		
ERM-Hong Kong, Limited		
O		
Approved by:	Frank Wan	
	Warch-AJ.	
Signed:		
Position:	Partner	
Certified by:	2	
	onmental Team Leader - Katie Yu)	
Date:	18 October 2017	

This report has been prepared by ERM-Hong Kong, Limited with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client.

We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.

This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.



香港九龍尖沙咀海港城 九倉電訊中心十三樓 13/F Wharf T&T Centre Harbour City Tsim Sha Tsui Kowloon Hong Kong

電話 Tel (852) 2972 1000 傳真 Fax (852) 2890 6343

info.hk@atkinsglobal.com www.atkinsglobal.com

Your ref. 0095646_let_Atkins_20171018 Quarterly EM&A Report No.23.doc

Our ref. 5121189/17.20/OC129/KC/EK

Date: 23 October 2017

By Post and Email (katie.yu@erm.com)

ERM-Hong Kong Limited, 16/F Berkshire House, 25 Westlands Road, Quarry Bay, Hong Kong

Attn: Ms Katie Yu

Dear Katie,

Central Police Station Conservation and Revitalization Project Verification of Quarterly EM&A Report No. 23

We refer to your letter dated 18 October 2017 regarding the Quarterly EM&A Report No. 23. Atkins China Limited verifies, in the capacity of Independent Environmental Checker, that the report conforms the requirements provided in Section 10.4 of the EM&A Manual.

Yours sincerely, For Atkins China Limited

Keith Chau Independent Environmental Checker

c.c. HKJC – Mr. Kenneth Lee (By Email)
Rocco Design Architect – Mr. Charles Kung (By Email)

CONTENTS

	EXECUTIVE SUMMARY	I
1	INTRODUCTION	1
1.1	PURPOSE OF THE REPORT	1
1.2	STRUCTURE OF THE REPORT	1
2	PROJECT INFORMATION	3
2.1	BACKGROUND	3
2.2	SITE DESCRIPTION	3
2.3	CONSTRUCTION ACTIVITIES	3
2.4	CONSTRUCTION PROGRAMME	4
2.5	PROJECT ORGANISATION AND MANAGEMENT STRUCTURE	4
2.6	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	4
3	ENVIRONMENTAL MONITORING REQUIREMENTS	6
3.1	Noise Monitoring	6
3.2	CULTURAL HERITAGE	8
3.3	LANDSCAPE AND VISUAL MONITORING	9
3.4	ENVIRONMENTAL REQUIREMENTS IN CONTRACT DOCUMENTS	9
4	IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES	I 10
5	MONITORING RESULTS	11
5.1	Noise	11
5.2	LANDSCAPE AND VISUAL MONITORING	11
5.3	CULTURAL HERITAGE	13
5.4	WASTE MANAGEMENT	16
5.5	EFFECTIVENESS OF MITIGATION MEASURES AND MONITORING	17
6	ENVIRONMENTAL SITE INSPECTION	18
7	ENVIRONMENTAL NON-CONFORMANCE	20
8	REVIEW OF THE EM&A DATA AND EIA PREDICTIONS	22
8.1	NOISE	22
<i>8.</i> 2	WASTE MANAGEMENT	22
8.3	SUMMARY OF REVIEW	23
9	CONCLUSIONS	24

LIST OF TABLES

Table 2.1	Summary of Construction Activities undertaken in this Reporting Period
Table 2.2	Summary of Environmental Licensing, Notification and Permit Status
Table 3.1	Construction Phase Noise Monitoring Locations
Table 3.2	Noise Monitoring Equipment
Table 3.3	Action and Limit Levels for Construction Noise Monitoring
Table 3.4	Alert, Alarm and Action (AAA) Levels for Vibration Monitoring
Table 3.5	Event and Action Plan for vibration monitoring
Table 4.1	Status of Required Submissions
Table 5.1	Findings of Monthly Tree Inspection in the Reporting Period
Table 5.2	Quantities of Waste Generated from the Project
Table 8.1	Comparison of Construction Noise Standard and Noise Monitoring Results
Table 8.2	Quantity of Actual Amount of C&D Materials, General Wastes and Chemical
	Wastes Generated and EIA Estimation
	LIST OF ANNEXES

Annex A	Locations of Works Areas and the Surroundings
Annex A1	Project Location
Annex A2	Declared Monuments within the Project Site
Annex A3	Site Layout Plan marked with Works
Annex B	Project Organization Chart and Contact Detail
Annex C	Locations of Noise Monitoring Stations and Noise Sensitive Receivers
Annex D	Monitoring Schedule of the Reporting Period
Annex E	Calibration Reports for Calibrators and Sound Level Meters
Annex F	Event/Action Plans for Noise
Annex G	Summary of Implementation Status
Annex H	Noise Monitoring Results
Annex I	Construction Programme of the Project
Annex J	Waste Flow Table
Annex K	Environmental Complaint, Environmental Summons and Prosecution Log
Annex L	Records of Vibration Monitoring for Other Construction Works
Annex M	Non-compliance Reports and Summary of Condition of Character Defining
	Elements, Historic Buildings and Structures
Annex M1	Non-compliance Reports
Annex M2	A Summary of Condition of Character Defining Elements, Historic Buildings and Structures

EXECUTIVE SUMMARY

The construction works of **Central Police Station Conservation and Revitalisation Project** commenced on 24 October 2011. This is the 23rd quarterly Environmental Monitoring and Audit (EM&A) summary report presenting the EM&A works carried out during the period from 1 May 2017 to 31 July 2017 in accordance with the EM&A Manual.

Environmental Monitoring and Audit Progress

A summary of the monitoring activities undertaken in this reporting period is listed below:

•	Construction Noise Monitoring during normal weekdays at	
	each monitoring station	16 times
•	Joint Environmental Site Inspection	3 times
•	Heritage Site Inspection	75 times
•	Landscape & Visual Monitoring / tree inspection	3 times
•	Vibration monitoring for other construction works	75 times

Noise

16 sets of 30-minute construction noise measurements were carried out at each of the monitoring stations (NM2 and NM6) during normal weekdays of the reporting period.

No exceedance of the Action or Limit Level of construction noise was recorded during the reporting period.

Cultural Heritage

No vibration monitoring was carried out for demolition works, trial piling or pile/bored piling works as the aforementioned works were not conducted during the reporting period.

Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

• 75 vibration monitoring measurements for the structural addition and alteration works at Block 11.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

75 heritage site inspections were conducted and the Contractor has generally implemented the necessary protection measures as recommended.

Landscape & Visual

Landscape and visual monitoring has commenced since October 2011 on a monthly basis. Three monthly tree inspections have been conducted by the arborist during the reporting period. The recommended actions have been performed by the Contractor as advised in the reporting period.

Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. 201.54 tonnes of inert C&D materials and 225.38 tonnes of non-inert C&D materials were generated during the reporting period. No metal, paper/cardboard or plastics waste was recycled during the reporting period. No chemical waste was collected by licenced chemical waste collector during the reporting period.

Environmental Site Inspection

Three joint environmental site inspections were carried out by the representatives of the Contractor, the IEC and the ET during the reporting period. Key observations and recommendations identified during the monthly site inspections were rectified by the Contractor in the subsequent monthly site inspections.

Environmental Exceedance/Non-conformance/Compliant/Summons and Prosecution

No exceedance of the Action or Limit Level of construction noise was recorded at designated monitoring stations during the reporting period.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

One enquiry was received during the reporting period.

No environmental non-compliance event was recorded during the reporting period. Two non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period.

No complaint was received during the reporting period.

No summons/prosecution was received in this reporting period.

1 INTRODUCTION

ERM-Hong Kong, Limited (ERM) was appointed by the Jockey Club CPS Limited (the CPS Ltd) as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the **Central Police Station Conservation and Revitalisation Project** (the Project).

1.1 Purpose of the Report

This is the 23rd quarterly EM&A summary report, which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from 1 May 2017 and 31 July 2017.

1.2 STRUCTURE OF THE REPORT

The structure of the report is as follows:

Section 1: **Introduction**

details the scope and structure of the report.

Section 2: **Project Information**

summarises background and scope of the Project, site description, project organization and contract details, construction programme, the construction works undertaken and the status of Environmental Permit(s)/License(s) during the reporting period.

Section 3: Environmental Monitoring Requirements

summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event/Action Plans, environmental mitigation measures as recommended in the EIA report, and relevant environmental requirements.

Section 4: **Implementation Status on Environmental Mitigation Measures** summarises the implementation of environmental protection measures during the reporting period.

Section 5: **Monitoring Results**

summarises the monitoring and waste management results obtained in the reporting period.

Section 6: Environmental Site Inspection

summarises the audit findings of the monthly site inspections undertaken within the reporting period.

Section 7 : **Environmental Non-conformance** summarises any monitoring exceedance, environmental complaints and environmental summons received within the reporting period.

Section 8 : **Review of the EM&A Data and EIA Predictions** compares the monitoring data and waste quantity against predictions in the approved Project EIA report.

Section 9: Conclusions

2 PROJECT INFORMATION

2.1 BACKGROUND

The Chief Executive (CE)'s 2007-2008 Policy Address highlighted revitalisation as the guiding principle of heritage conservation and the Project was among one of the specific proposals put forward by the CE in the same Policy Address. At the meeting of the Executive Council (ExCo) on 15 July 2008, the ExCo advised and the CE ordered that Government should enter into a partnership with the Hong Kong Jockey Club (HKJC) in the form of an agreement (or agreements) to take forward the conservation and revitalisation of the CPS project based on various guiding parameters. The Project is now being undertaken in partnership with the Development Bureau of the HKSAR Government. The HKJC has taken on board the decision at the ExCo meeting and further investigated the design and implementation of the Project. The Project is now implemented by the Jockey Club CPS Limited.

2.2 SITE DESCRIPTION

The location of the Project Site is shown in *Annex A1*. The Site is bounded by Hollywood Road to the north, Arbuthnot Road to the east, Chancery Lane to the south and Old Bailey Street to the west.

The Site comprises three Declared Monuments designated under the *Antiquities and Monuments Ordinance* in 1995. They are:

- Central Police Station;
- Former Central Magistracy; and
- Victoria Prison Compound.

They are collectively named the Central Police Station (CPS). *Annex A2* shows the location of the Declared Monuments within CPS and the buildings within the CPS.

2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in this reporting period is shown in *Table 2.1* and illustrated in *Annex A3*.

Table 2.1 Summary of Construction Activities undertaken in this Reporting Period

Construction Activities Undertaken

May 2017:

- Hard landscape construction;
- Timber elements repair and replacement at Blocks 1, 3, 6, 7, 9 and 13;
- Fitting out works at Blocks 1, 3, 6, 7, 9, 11, 14, 15, 17, Arbuthnot Wing and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 8, 9, 14 and 17;
- External façade repair at Blocks 3, 9, 10, 11, 13, 14 and 17;
- E&M fixing at Blocks 1, 3, 6, 7, 9, 12, 13, 14, 15, Arbuthnot Wing and Old Bailey Wing;
- Footbridge construction; and
- Old Bailey Street staircase construction.

June 2017:

- Sitewide hard landscape construction;
- Timber elements repair and replacement at Blocks 1, 3, 6, 7, 9 and 14;
- Fitting out works at Blocks 1, 3, 6, 7, 9, 11, 14, 15, 17, Arbuthnot Wing and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 8, 9, 14 and 17;
- External façade repair at Blocks 3, 9, 10, 11, 13, 14 and 17;
- E&M fixing at Blocks 1, 3, 6, 7, 9, 12, 13, 14, 15, Arbuthnot Wing and Old Bailey Wing; and
- Footbridge construction.

July 2017:

- Sitewide hard landscape construction;
- Timber elements repair and replacement at Blocks 1, 3, 6, 7, 9 and 14;
- Fitting out works at Blocks 1, 3, 6, 7, 9, 11, 14, 15, 17, Arbuthnot Wing and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 8, 9 and 14;
- External façade repair at Blocks 3, 9, 10, 12, 13, 14 and 17;
- E&M fixing at Blocks 1, 3, 6, 7, 9, 12, 13, 14, 15, Arbuthnot Wing and Old Bailey Wing;
- Footbridge construction; and
- Enhancement works at Blocks 6 and 7.

2.4 CONSTRUCTION PROGRAMME

The most updated construction programme for the Project is presented in *Annex I*.

2.5 PROJECT ORGANISATION AND MANAGEMENT STRUCTURE

The Project organization chart, hotline number and contact details are shown in *Annex B*.

2.6 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the valid permits, licences, and/or notifications on environmental protection for this Project within the reporting period is presented in *Table 2.2*.

Table 2.2 Summary of Environmental Licensing, Notification and Permit Status

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Environmental Permit (EP)	EP-408/2011/C	Throughout the Contract	Permit granted on 29 April 2016
Notification of Construction Works as required under <i>Air</i> Pollution Control (Construction Dust) Regulation	Ref. No. 332920	Throughout the Contract	-
Registration of Chemical Waste Producer under Waste Disposal Ordinance	Chemical Waste Producer No.: 5213- 122-G2347-25	Throughout the Contract	-
Disposal of C&D material/waste	Billing Account Number: 7013338	Throughout the Contract	-
Effluent Discharge License under Water Pollution Control Ordinance	License No. WT00026824-2017	11 Jan 2017 – 31 Oct 2021	-
Notification of Commencement of Asbestos Abatement Work under Air Pollution Control Ordinance		Throughout the Contract	EPD's letter (EPD's ref.: (5) in EPAC/A/4/000/23 3 II) dated 2 December 2011 satisfied that the content of the asbestos abatement plan (Report No.: 0210/11/ED/0078A) is in accordance with the APCO
Approval of Asbestos Abatement Work (Phase 2)	-	Earliest commencement date on 26 January 2012	EPD's letter (EPD's ref:() in EPAC/A/4/000/23 3) dated 18 January 2012.
Construction Noise Permit (CNP)	GW-RS1270-16	15 December 2016 at 0000 hours to 11 June 2017 at 2400 hours	-
	GW-RS0443-17	12 June 2017 at 1900 hours to 10 December 2017 at 1800 hours	This CNP was cancelled and superseded by GW-RS0599-17 at 1900 hours on 17 July 2017.
	GW-RS0599-17	17 July 2017 at 1900 hours to 16 January 2018 at 2300 hours	-

ENVIRONMENTAL MONITORING REQUIREMENTS

3.1 Noise Monitoring

3

3.1.1 Monitoring Location

The construction noise monitoring locations are given in *Table 3.1* and shown in *Annex C*.

 Table 3.1
 Construction Phase Noise Monitoring Locations

Monitoring Location	Proposed Construction Noise Monitoring Station			
	ID in EM&A Manual	ID	Type of Measurement	Remark
Rooftop of Ho Fook Building	N2	NM2	Façade	-
Rooftop of Chancery Mansion		NM6	Façade	Accesses to the original proposed monitoring location in the EM&A Manual, Chancery House (N5), were rejected; alternative location of Chancery Mansion (N6), were therefore proposed and approved by the Authorised Person (AP), the Independent Environmental Checker (IEC) and EPD.

The noise sensitive receivers are also shown in *Annex C*.

3.1.2 *Monitoring Parameters, Frequency and Programme*

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. The monitoring programme for this reporting period is shown in *Annex D*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level (L_{eq}) in decibels dB(A). $L_{eq~(30min)}$ were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays. Supplementary information for data auditing, two statistical sound levels L_{10} and L_{90} ; the levels exceeded for 10 and 90 percent of the time respectively, were also recorded during the monitoring for reference. The measured noise levels were logged in every 5 minutes throughout the impact monitoring period.

3.1.3 Monitoring Equipment and Methodology

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures* of *Technical Memorandum on Noise from*

Construction Work other than Percussive Piling (GW-TM) issued under the Noise Control Ordinance (NCO) (Cap 400).

The sound level meters and calibrator used for the noise measurement, as listed in *Table 3.2*, complies with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters are included in *Annex E*.

Table 3.2 Noise Monitoring Equipment

Monitoring Stations	Monitoring Equipment (Sound Level Meter and Calibrator)
NM2, NM6	<u>Calibrator</u> CEL-120 (S/N 3421612)
	Sound Level Meter
	CEL-633A (S/N 3521757)

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

Measurements were accepted as the calibration level from before and after the noise measurement agree to within 1.0 dB.

3.1.4 Event/Action Plan

Table 3.3 Action and Limit Levels for Construction Noise Monitoring

Noise Monitoring Location	Action Level	Limit Level, L _{eq(30mins), dB(A)}	Remark
NM2, NM6	When one documented complaint is received from any one of the sensitive receivers	75 (note)	Applicable during 0700 – 1900 hours on normal weekdays.

Notes:

- a) Acceptable Noise Levels for Area Sensitivity Rating of A/B/C. Limit Level is reduced to 70dB(A) for schools and 65dB(A) during school examination periods.
- b) If works are to be carried out during restricted hours, the conditions stipulated in the CNP issued by the NCA have to be followed.

The Event / Action Plan (EAP) for noise monitoring is presented in *Annex F*.

3.1.5 Mitigation Measures

The mitigation measures in accordance with the EP, EIA and EM&A Manual and their implementation status are presented in *Annex G*.

3.2 CULTURAL HERITAGE

3.2.1 *Vibration Monitoring*

In accordance with the EM&A Manual, vibration monitoring is required and the vibration control limits and vibration monitoring proposal are defined by a specialist for AMO's approval.

Baseline Monitoring

Baseline vibration monitoring was not conducted during the reporting period.

Vibration Monitoring for Demolition Works

As no demolition works were carried out, vibration monitoring for demolition works was not conducted during the reporting period.

Vibration Monitoring for Trial Piling and Pipe/Bored Piling Works

As no trial piling or pipe/bored piling works were carried out, vibration monitoring for trial piling and pipe/bored piling works was not conducted during the reporting period.

Vibration Monitoring for Other Construction Works

Vibration monitoring for specific construction works other than demolition works, trial piling works and pipe/bored piling works is also required in accordance with Building Department's requirement. The monitoring location is shown in *Annex L*. The number and location of monitoring location will depend on the location of the specific construction works. The vibration monitoring should be conducted for duration of 5 minutes on a daily basis (working day) at each vibration monitoring location.

Alert, Alarm and Action Levels

The Alert, Alarm and Action (AAA) Levels are to be implemented during the vibration monitoring and shown in *Table 3.4*.

Table 3.4 Alert, Alarm and Action (AAA) Levels for Vibration Monitoring

Instrument Type	Item Monitored	Alert Level	Alarm Level	Action Level
Vibration Monitoring	Horizontal Movement	2.0 mm/s	2.5 mm/s	3.0 mm/s

The Event / Action Plan (EAP) for vibration monitoring is shown in *Table 3.5*.

Table 3.5 Event and Action Plan for Vibration Monitoring

Events	Action
Exceedance of Alert Level	Notify Management Contractor
Exceedance of Alarm Level	Notify Authorised Person/ Resident Engineer

Events	Action
Exceedance of Action Level	Cease Works and submit mitigation

3.2.2 *Mitigation Measures*

Cultural heritage mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

3.3 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, inspections of affected trees were conducted by an experienced and appropriately trained arborist. All irregularities that deviate from the recommended tree protection measures or could impose deleterious impacts on the protected trees were reported. Besides, implementation of mitigation measures for landscape and visual resources recommended in the EIA Report were also monitored during the site inspection.

3.3.1 *Mitigation Measures*

Landscape and visual mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

3.4 ENVIRONMENTAL REQUIREMENTS IN CONTRACT DOCUMENTS

The environmental requirements as specified in the contract documents were reviewed and were covered in the EIA's requirements.

4 IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES

The Contractor has generally implemented the environmental mitigation measures (including those for archaeology) and requirements as stated in the EIA Report, EM&A Manual, EP and the contract documents. The implementation status during the reporting period is summarised in *Annex G*.

Status of required submissions under the EP during the reporting period is presented in *Table 4.1*.

Table 4.1 Status of Required Submissions

Submission		Submission Date
EP Condition		
Conditions 3.4	66 th Monthly EM&A Report	12 May 2017
	• 67th Monthly EM&A Report	14 June 2017
	• 68th Monthly EM&A Report	14 July 2017
EM&A Manual		
Section 10.4	• 22 nd Quarterly EM&A Report	4 July 2017
Section 10.5	• 5 th Annual EM&A Report	23 May 2017

MONITORING RESULTS

5.1 Noise

5

A total of 16 sets of 30-minute construction noise measurements were carried out at each monitoring station, NM2 and NM6, during normal weekdays of the reporting period. The monitoring results together with graphical presentations are presented in *Annex H*. The local impacts observed near the monitoring stations of NM2 and NM6 were summarised below:

- NM2: construction noise from activities in the Project Site and traffic noise from Old Bailey Street.
- NM6: construction noise from activities in the Project Site and traffic noise from Chancery Lane.

No exceedance of the Action or Limit Level of construction noise was recorded during the reporting period.

5.2 LANDSCAPE AND VISUAL MONITORING

Three monthly tree inspections were conducted by the arborist during the reporting period on 5 May 2017, 8 June 2017 and 10 July 2017 and key findings and recommendations are summarised in *Table 5.1*.

Table 5.1 Findings of Monthly Tree Inspections in the Reporting Period

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observation / Recommendations
5 May 201	7		
Tree -5	Mangifera indica	Fair	The Contractor should erect a Tree Protection Zone at the planter as repairing of the planter is nearly completed.
Tree -6	Aleurites moluccana	Fair	 The Contractor should add more mulch and erect a Tree Protection Zone at the planter.
Tree-7	Aleurites moluccana	Fair	 The Contractor should add more mulch and erect a Tree Protection Zone at the planter.
Tree-8	Plumeria rubra	Fair	 The Contractor should add more mulch and erect a Tree Protection Zone at the planter.
Tree-9	Araucaria cunninghamia	Fair	 The Contractor should add more mulch and erect a Tree Protection Zone at the planter.
Tree-11	Dracaena marginata	Fair	 The Contractor should closely monitor the growth of the tree.
8 June 201	7		

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observation / Recommendations
Tree -5	Mangifera indica	Fair	No further action is required.
Tree -6	Aleurites moluccana	Fair	 A tree protection zone has been erected to protect the tree.
			Add more mulch at the planter.
Tree-7	Aleurites moluccana	Fair	 A tree protection zone has been erected to protect the tree.
			Add more mulch at the planter.
Tree-8	Plumeria rubra	Fair	 A tree protection zone has been erected to protect the tree.
			 Add more mulch at the planter.
Tree-9	Araucaria cunninghamia	Fair	 A tree protection zone has been erected to protect the tree.
			 Add more mulch at the planter.
Tree-11	Dracaena marginata	Fair	 Remove construction debris away from the planter
			 The Contractor should closely monitor the growth of the tree.
10 July 20	17		
Tree -5	Mangifera indica	Fair	 No further action is required.
Tree -6	Aleurites moluccana	Fair	 Reasonable amount of mulch has been added to the planter.
			 Signs of pest (<i>Trialeurodes</i> vaporariorum) have been observed on the faded leaves.
			 Application of pesticides to the tree should be carried out as soon as possible.
Tree-7	Aleurites moluccana	Fair	 Reasonable amount of mulch has been added to the planter.
			 A decayed log has been observed on the upper branches.
			 Signs of pest (<i>Trialeurodes</i> vaporariorum) have been observed on the faded leaves.
			 Application of pesticides to the tree and puning of the decayed log should be carried out as soon as possible.
Tree-8	Plumeria rubra	Good	 No further action required.
Tree-9	Araucaria cunninghamia	Good	No further action required.
Tree-11	Dracaena marginata	Fair	 Remove construction debris away from the planter
			 The planter was observed to be covered with construction dust.
			 To wrap the trunk with hessian cloth and to add more hessian cloth to cover the planter.
			 Withered leaves were observed on the tree.

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observation / Recommendations
			The Contractor should closely monitor the growth of the tree.

Follow-up actions needed to be implemented were recommended to the Contractor and the status of the follow-up actions was reviewed during the subsequent monthly site inspections. Recommendations have generally been implemented by the Contractor during the reporting period.

5.3 CULTURAL HERITAGE

5.3.1 Vibration Monitoring

No vibration monitoring was carried out for demolition works, trial piling or pile/bored piling works as the aforementioned works were not conducted during the reporting period.

Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

May 2017:

• 24 vibration monitoring measurements for the structural addition and alteration works at Block 11.

June 2017:

• 26 vibration monitoring measurements for the structural addition and alteration works at Block 11.

July 2017:

• 25 vibration monitoring measurements for the structural addition and alteration works at Block 11.

The monitoring results are presented in *Annex L*.

All monitoring results were below the Alert/Alarm/ Action Levels during the reporting period.

5.3.2 Heritage Site Audit

Heritage site audits were conducted on every working weekday by the Heritage Checker during the reporting period. Key site audit findings and recommendations are summarised below. The Contractor was urged to follow-up the necessary rectification based on the inspection findings.

17 May 2017

• Lack of site control and supervision during excavation on ground floor of Block 3 was observed. The Contractor was reminded to ensure that all site operations are planned and sequenced to complete the works in the most efficient and safe manner.

25 May 2017

• The chimney at Block 13 was observed to be left in an unsafe situation after canopy demolition. The Contractor was reminded to provide immediate propping and closely supervise the demolition work.

29 May 2017

• External render was observed to be cracked after the installation of glass balustrade. The Contractor was reminded to provide protective measures and assess the area of damage.

31 May 2017

- It was observed that the wall and door frame was damaged on ground floor at Block 14. The Contractor was reminded to follow up and provide sufficient supervision.
- It was observed that some new metal doors (14/DLG/21, 22, 23) on lower ground of Block 14 was not fabricated. The Contractor was reminded to rectify the incorrect doors.
- It was observed that the protection to existing door at Block 14 ground floor was missing. The Contractor was reminded to follow up and provide sufficient protection.
- It was observed that there was lack of care to historic windows. The Contractor was reminded to increase site supervision and briefing and provide sufficient protection.
- It was observed that the protection to painted sign at Block 15 was missing. The Contractor was reminded to follow up and provide sufficient protection to the painted sign.
- It was observed that the protection to surrounding building fabric at Block 14 lower ground during excavation was missing. The Contractor was reminded to follow up and provide sufficient protection.
- Animal decomposition was observed at Block 14 external staircase. The Contractor was reminded to clean up this area and ensure hygiene condition on site.
- It was necessary to improve the cleanness at Block 7 after construction works. The Contractor was reminded to provide regular tidy-up.

- Temporary plywood protection was observed to be rotten. The Contractor was reminded to follow up and replace the rotten plywood protection.
- Protection barrier was observing missing during excavation. The Contractor was reminded to follow up and set up barriers for excavation.

8 June 2017

• It was observed that the tactile warning strip at Block 3 was not installed in accordance with the instructions. The Contractor was reminded to follow up and re-install the tactile warning strips.

9 June 2017

• It was observed that the scaffold was placed on the glazed tiles and that the tiles were not protected at Block 9. The Contractor was reminded to follow up and provide protection to the historic ceramic tiles and avoid damage to the tiles.

19 June 2017

• It was observed that there was no protection in place during glass balustrade installation at Block 9. Excessive grouting was observed on tiles and walls. The Contractor was reminded to follow up and rectify concrete grouting on tiles and walls as well as to improve site supervision.

29 June 2017

• It was observed that improvement of workmanship was required for the handrail replacement work at Block 3. The Contractor was reminded to follow up.

30 June 2017

- It was observed that the protection to painted sign at Block 7 was missing. The Contractor was reminded to follow up and provide sufficient protection to the painted sign.
- It was observed that vegetation was growing on the building façade of Block 6 and 7. The Contractor was reminded to follow up.
- Improvement on cleanliness and protection to tiles were required on ground floor toilet of Block 14. The Contractor was reminded to clean up the area and provide protection to the tiles.
- It was observed that improvement on tidiness at Sergeants' Yard was required. The Contractor was reminded to follow up.

6 July 2017

• It was observed that the external downpipe and timber windows at Block 6 were not decorated properly. The Contractor was reminded to follow up and re-decorate the downpipes.

31 July 2017

• It was observed that a number of new metal doors (14/DLG/21, 22, 23) at Block 14 lower ground level have not been fabricated in accordance with the approved drawings. The Contractor was reminded to follow up and rectify the metal doors.

Two non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period. The summary of condition of the character defining elements, historic buildings and structures as well as the non-compliance reports are contained in *Annex M*.

5.4 WASTE MANAGEMENT

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. Non-inert C&D materials were made up of wastes such as general refuse and mixed construction waste. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in *Table 5.2*. The summary of Waste Flow Table prepared by the Contractor is shown in *Annex J*. No metal, paper/cardboard packaging or plastic waste was recycled during the reporting period. No chemical waste was collected by licenced chemical waste collector during the reporting period.

Table 5.2 Quantities of Waste Generated from the Project

Month / Year	Quantity						
	C&D	C&D	Chemical		Recycled materials		
	Materials	Materials	Waste				
	(inert)	(non-inert)	Liquid	Solid	Paper/	Plastics	Metals
	(tonnes) (a)	(tonnes) (b)	(L)	(kg)	cardboard (kg)	(kg)	(kg)
May 2017	54.34	87.19	0	0	0	0	0
June 2017	134.59	80.65	0	0	0	0	0
July 2017	12.61	57.54	0	0	0	0	0
Total	201.54	225.38	0	0	0	0	0

Notes:

- (a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. The inert C&D materials were sent to Chai Wan Public Fill Barging Point, Tseung Kwan O Area 137 Fill Bank and Tuen Mun 38 Fill Bank.
- (b) Non-inert C&D materials include general refuse and mixed construction waste. The non-inert C&D materials were disposed of at SENT Landfill, Tseung Kwan O Area 137 Sorting Facility, Tuen Mun 38 Sorting Facility and NENT Landfill.

5.5 EFFECTIVENESS OF MITIGATION MEASURES AND MONITORING

The mitigation measures recommended in the EIA report and required by the EP are considered effective in minimising environmental impacts.

The EM&A for the Project was conducted as scheduled during the reporting period. No non-compliance events were observed during site inspections and no exceedances of action or limit level were recorded during the reporting period. The EM&A programme is considered effective.

6 ENVIRONMENTAL SITE INSPECTION

Three monthly environmental site inspections were conducted on 25 May 2017, 15 June 2017 and 18 July 2017 during the reporting period. There was no non-compliance recorded during the site inspections. Key observations and recommendations are summarised below. The recommendations were implemented and the observations were rectified by the Contractor in the subsequent monthly site inspection.

25 May 2017

• It was observed that over 20 bags of cement were stored near Block 3, some of them opened without covered by impervious sheet. The Contractor was reminded to provide impervious sheet to the cement bags after use.

15 June 2017

 Noise label for the air compressor located near Block 14 was observed missing. The Contractor was reminded to provide and attach appropriate noise label for the air compressor.

18 July 2017

• Nil

This page is deliberately left blank

7 ENVIRONMENTAL NON-CONFORMANCE

7.1.1 Summary of Monitoring Exceedance

No exceedance of the Action or Limit Level of construction noise or Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

7.1.2 Summary of Enquiry

One enquiry was recorded during the reporting period. Ming Pao, a Chinese newspaper in Hong Kong, has published an article on 31 July 2017 indicating that the abundance of leaves on Tree 6 and Tree 7 has seemingly reduced in comparison with the photos of the trees taken in December 2015 and pests were found in both trees. An investigation is currently being carried out to address the Ming Pao report and the investigation report will be provided in the next reporting period.

7.1.3 Summary of Non-Compliance

No environmental non-compliance event was recorded during the reporting period. Two non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period and are presented in *Annex M*.

7.1.4 Summary of Environmental Complaint

No complaint was received during the reporting period. The cumulative number of complaints is presented in *Annex K*.

7.1.5 Summary of Environmental Summons and Successful Prosecution

No summons was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex K*.

This page is deliberately left blank

8.1 NOISE

A comparison was made between the monitoring results in this reporting period and the Noise Standard for general construction works during 0700 – 1900 hrs on normal weekdays (*Table 8.1*).

Table 8.1 Comparison of Construction Noise Standard and Noise Monitoring Results

Reporting Month	Monitoring Stations	Corresponding NSR in EIA	Noise Limit Level	Predicted Construction Noise Level (With Mitigation) in EIA	Measured Construction Noise Level
			L _{eq, 30 min} dB(A)	L _{eq, 30 min} dB(A)	L _{eq, 30 min} dB(A)
May 2017	NM2	N2	75	67 - 72	67.5 – 70.6
	NM6	N6	75	73 - 75	64.3 - 67.5
June 2017	NM2	N2	75	67 - 72	66.3 - 71.0
	NM6	N6	75	73 - 75	62.7 - 66.7
July 2017	NM2	N2	75	67 - 72	64.0 - 67.5
	NM6	N6	75	73 - 75	63.3 - 68.3

The monitoring results recorded since the commencement of the construction works have been below the Limit Level and comparable to the predicted construction noise level in the approved EIA. Recommended mitigation measures in *Section 5.9.1* of EIA will continue to be implemented throughout the construction stage.

8.2 WASTE MANAGEMENT

The estimated amount of waste generated in the approved EIA and the accumulated quantities of waste generated up to this reporting period are presented in *Table 8.2*. The accumulated amount of inert and non-inert C&D materials is higher than the estimated amount in EIA. The major chemical waste generated on site was primarily asbestos which was not estimated in the approved EIA and hence no data is available for comparison. Recommended mitigation measures in *Section 8.5.1* of the EIA will continue to be implemented throughout the construction stage.

Table 8.2 Quantity of Actual Amount of C&D Materials, General Wastes and Chemical Wastes Generated and EIA Estimation

Type of Material	Estimated Amount of Waste in EIA	Accumulated Actual Amount of Waste Recorded ^(a) ^(b)
Amount of C&D Materials (Inert) Arising	16,440 m ³	37,674.0 m ³
Amount of C&D Materials (Non-inert) Arising	890 m ³	15,278.25 m ³
General Refuse	130 kg per day	_ (c)
Chemical Waste	Less than 100L per month	57 L (liquid)395 kg (solid)7,000 kg of asbestos generated

Notes:

- (a) The accumulated actual amount of C&D Materials and chemical waste were recorded since the commencement of construction works.
- (b) The volume of waste materials are provided by the Contractor based on the updated waste record in July 2017.
- (c) The amount of general refuse generated was not recorded.

8.3 SUMMARY OF REVIEW

The EIA predictions and the monitoring results since the commencement of construction works have been reviewed. The EIA concluded that the Project would not cause adverse impacts to the environment and the monitoring results have also indicated the same so far. Mitigation measures (including those for archaeology) recommended in the EP, EIA and EM&A Manual were implemented by the Contractor as far as practicable and were considered effective. The recommended mitigation measures will continue to be implemented throughout the construction phase of the Project.

The effectiveness of the monitoring programme has been exhibited therefore change to the programme is not considered to be necessary.

9 CONCLUSIONS

This 23rd Quarterly EM&A Report presents the EM&A works undertaken during the reporting period from 1 May 2017 to 31 July 2017 in accordance with the EM&A Manual.

No exceedance of the Action or Limit Level of construction noise was recorded at designated monitoring stations during the reporting period.

Tree inspections were conducted in this reporting period. Most of the necessary landscape and visual mitigation measures recommended in the EIA Report were implemented by the Contractor.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

One enquiry was received during the reporting period.

No environmental non-compliance event was recorded during the reporting period. Two non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period.


No complaint was received during the reporting period.


No summons/prosecution was received during the reporting period.

The monitoring programme was considered effective in reflecting the environmental conditions at the designated representative sensitive receivers. The monitoring results also indicate that the Project have not caused adverse impacts on the environment with implementation of appropriate mitigation measures. Change to the monitoring programme is not considered to be necessary. The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures in the coming periods.

Annex A

Locations of Works Areas and the Surroundings

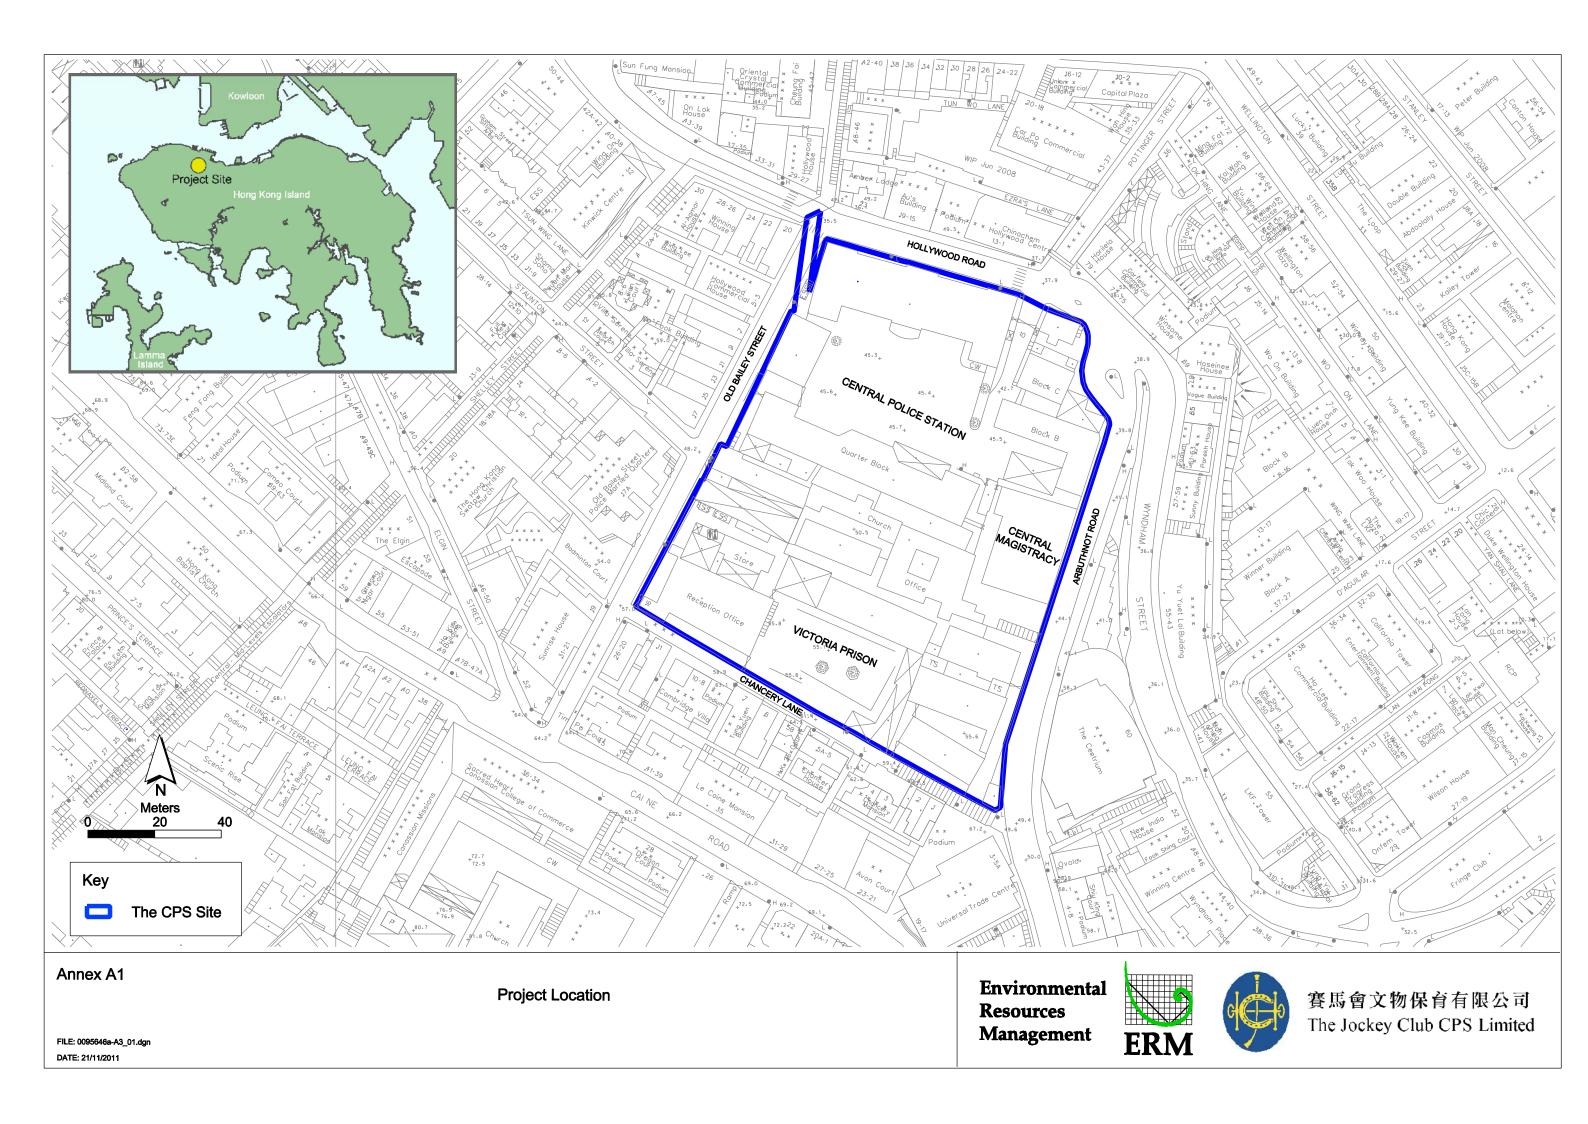

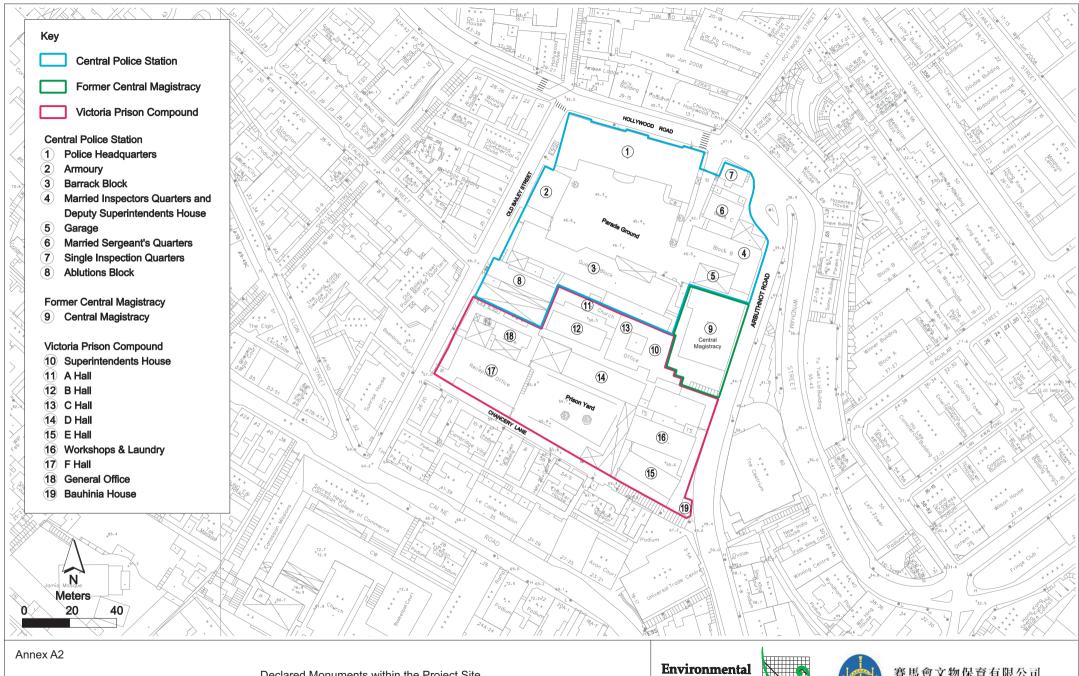


FILE: 0095646b1-A3.dgn DATE: 07/12/2011


Declared Monuments within the Project Site


Resources Management





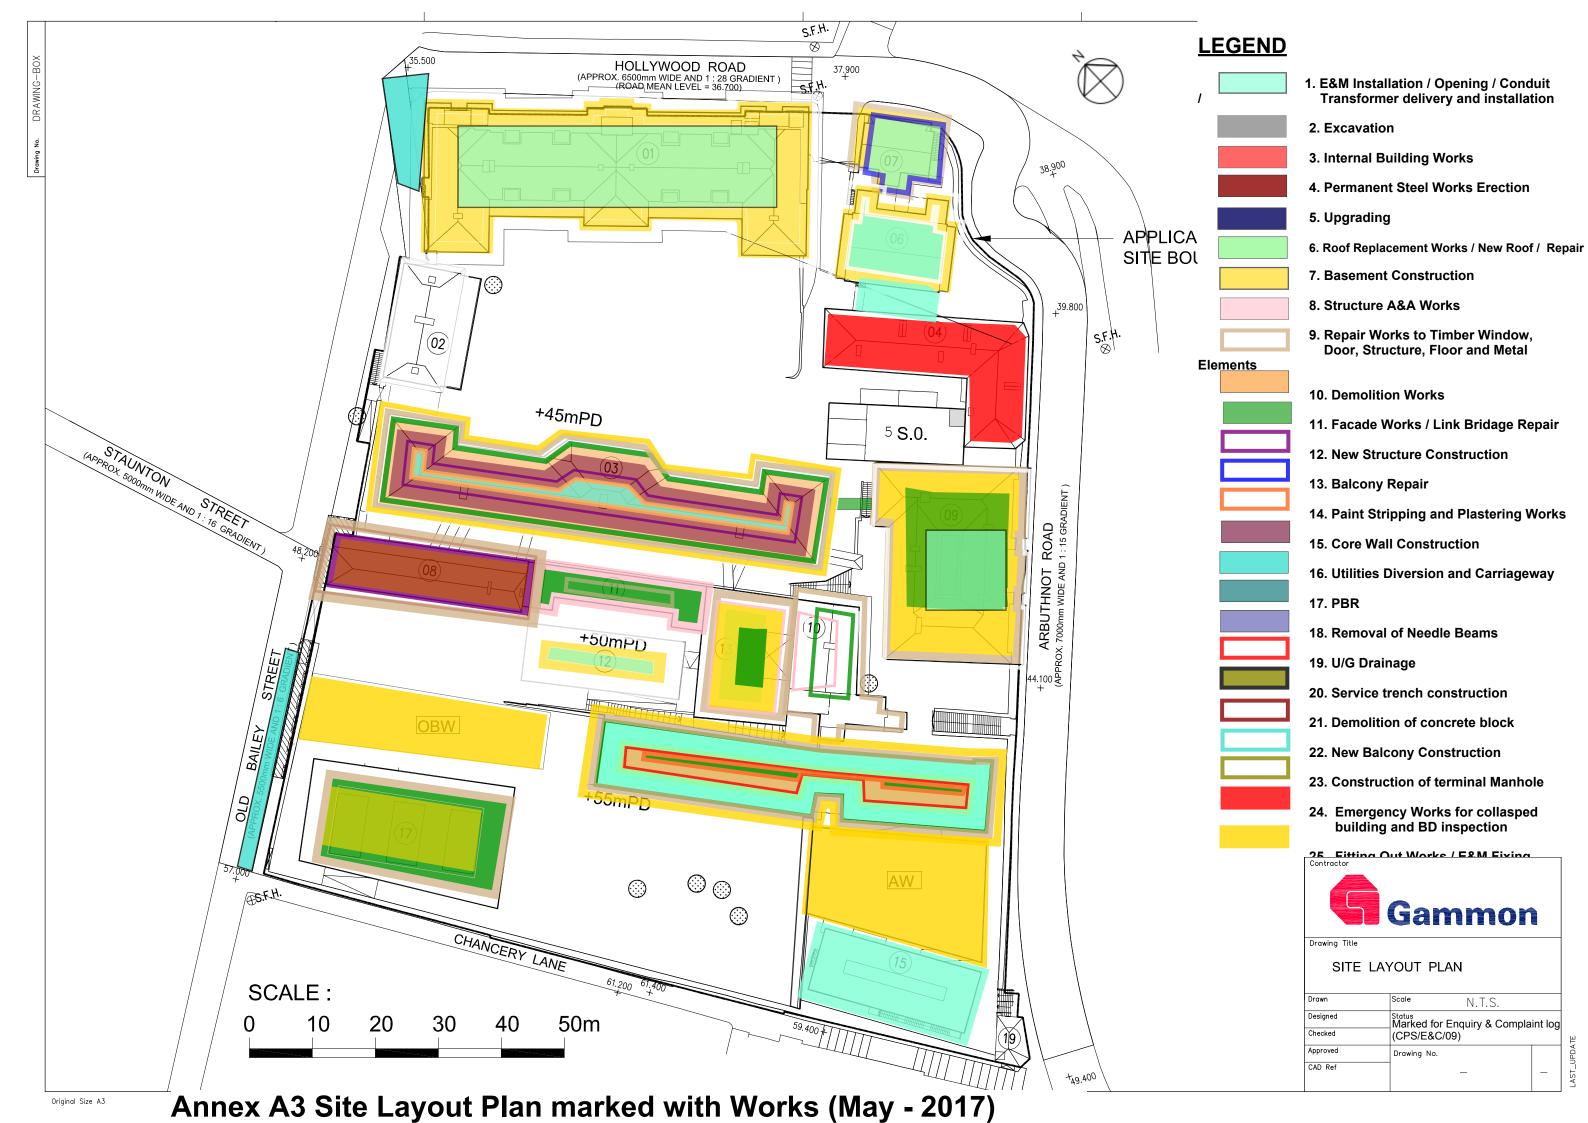


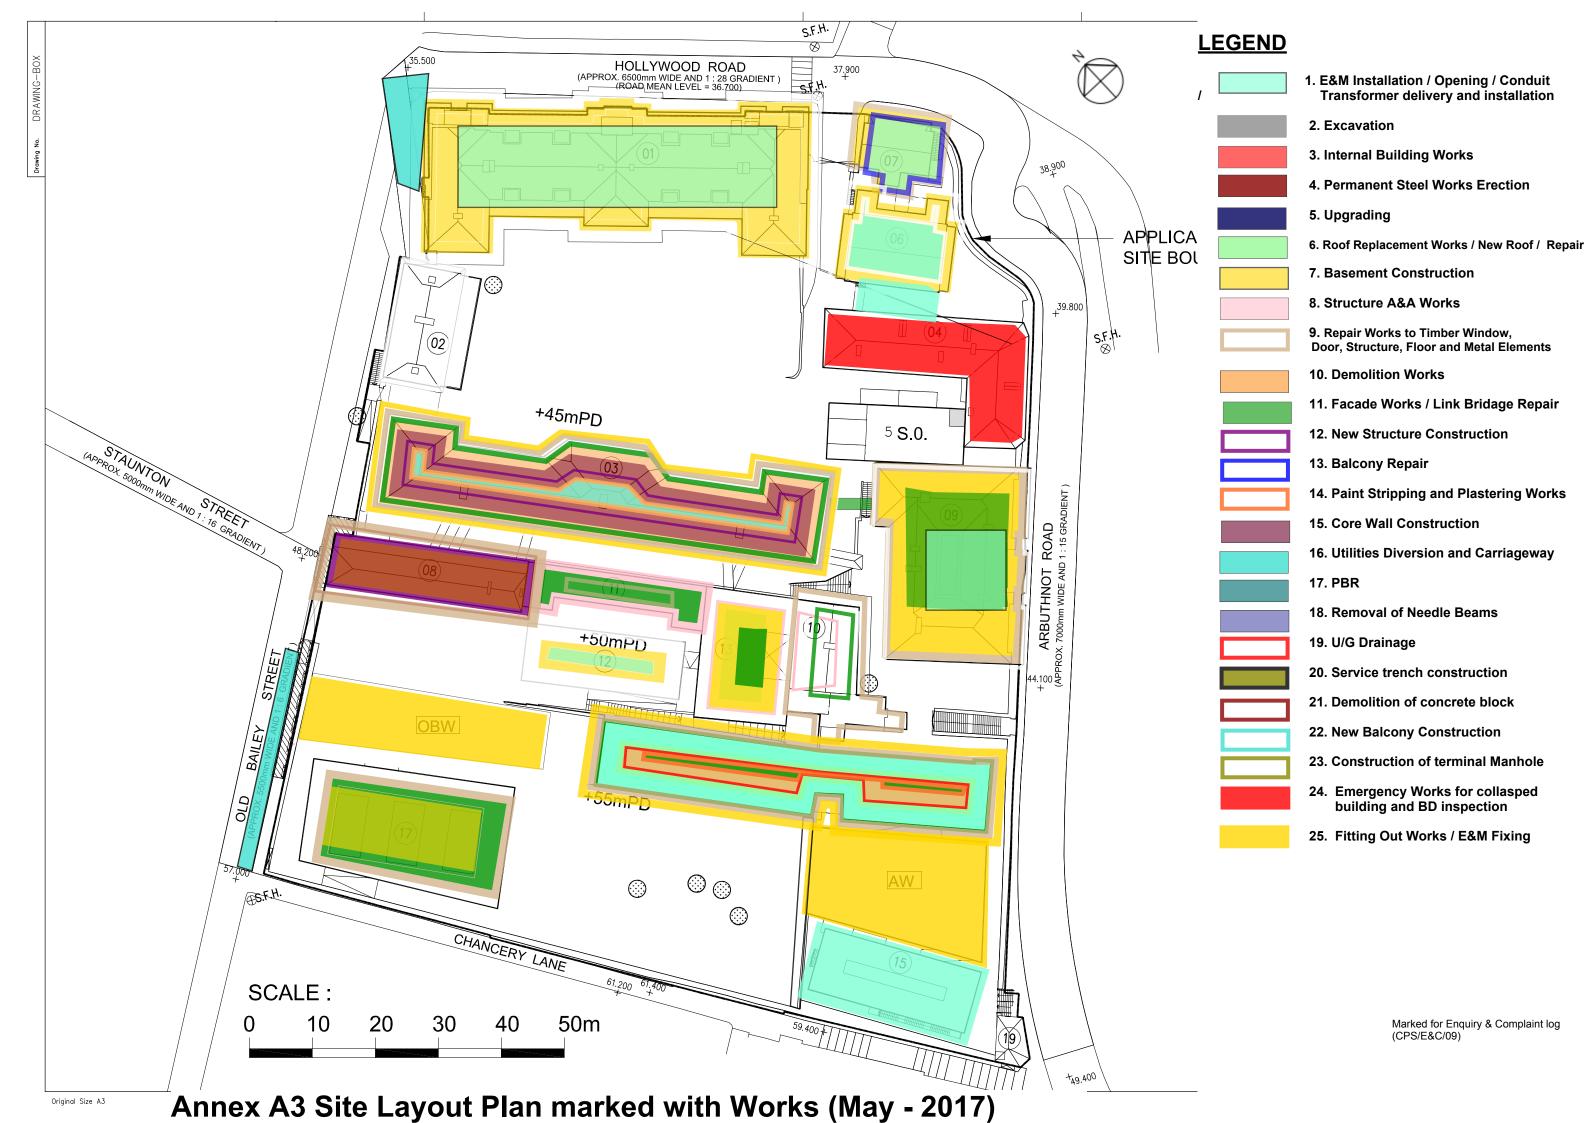

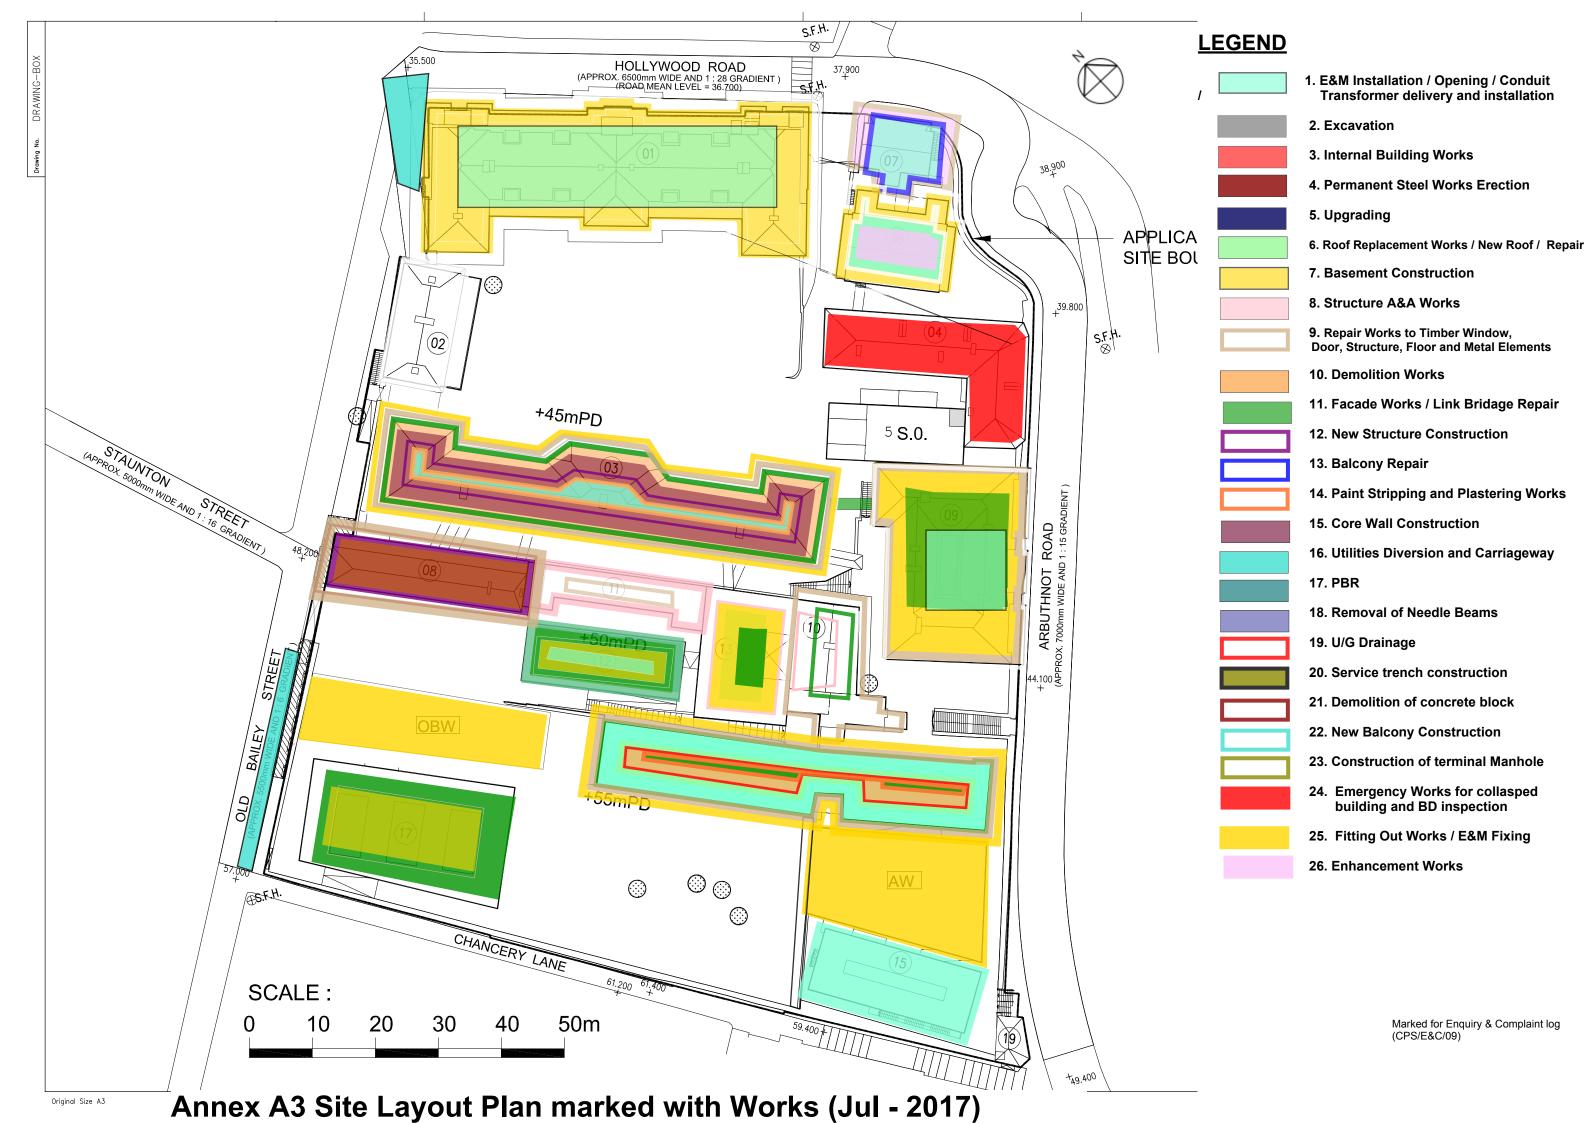


Annex B

Project Organization Chart and Contact Detail

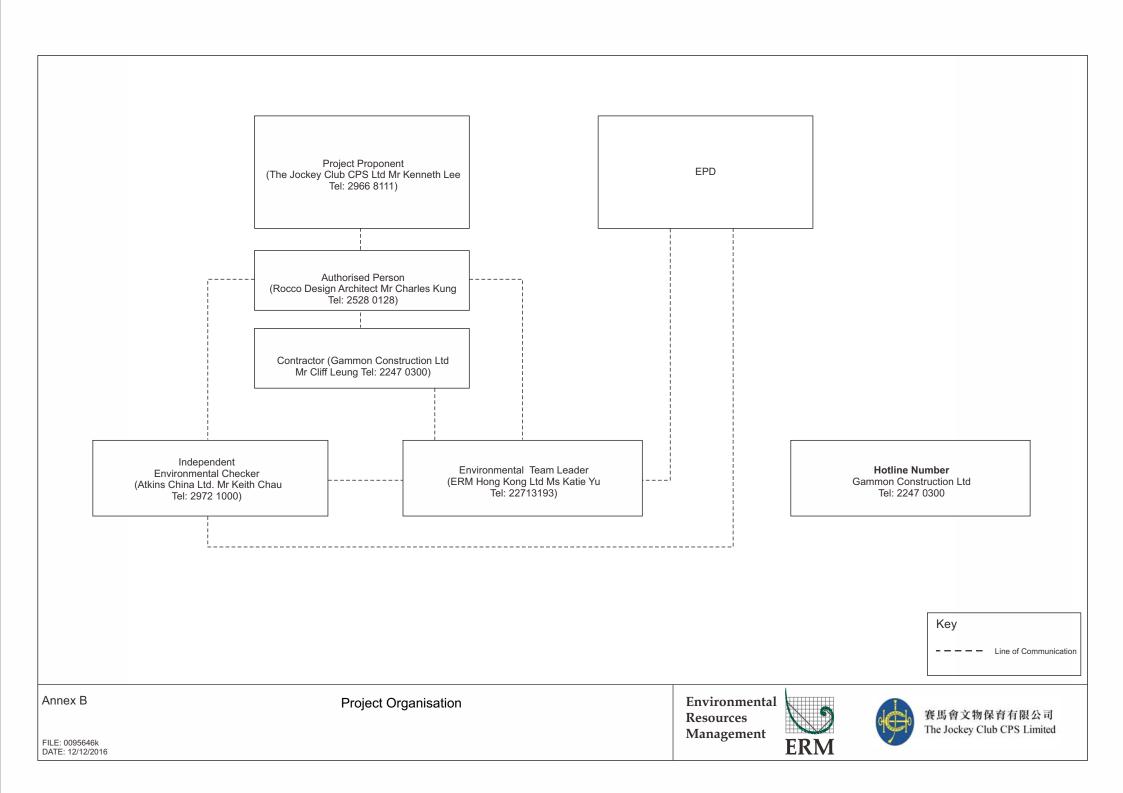

Annex C

Locations of Noise Monitoring Stations and Noise Sensitive Receivers

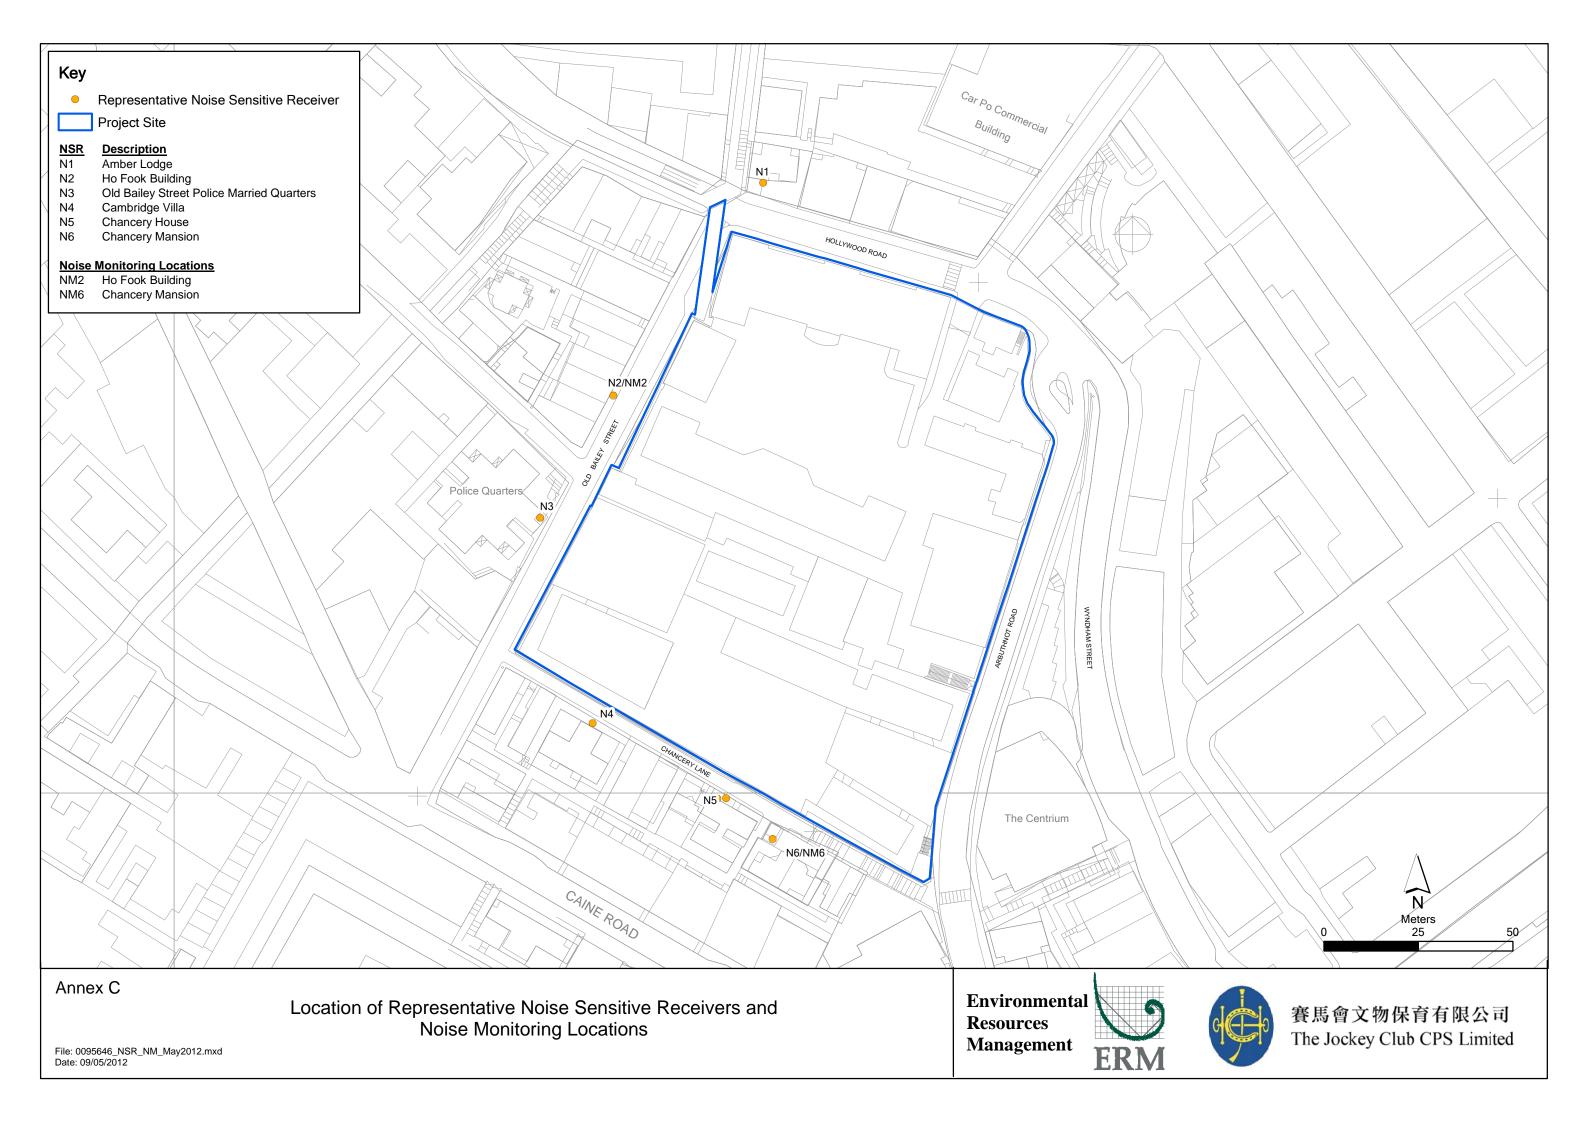

Annex D

Monitoring Schedule of the Reporting Period and Next Month

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - May 2017

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	01-May	02-May	03-May	04-May	05-May	06-May
	Public Holiday		Public Holiday		Noise Monitoring at NM2 & NM6	
07-May	08-May	09-May	10-May	11-May	12-May	13-May
				Noise Monitoring at NM2 & NM6		
14-May	15-May	16-May	17-May	18-May	19-May	20-May
			Noise Monitoring at NM2 & NM6			
21-May	22-May	23-May	24-May	25-May	26-May	27-May
		Noise Monitoring at NM2 & NM6				
28-May	29-May	30-May	31-May			
	Noise Monitoring at NM2 & NM6					

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - June 2017

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				01-Jun	02-Jun	03-Jun
					Noise Monitoring at NM2 & NM6	
04-Jun	05-Jun	06-Jun	07-Jun	08-Jun	09-Jun	10-Jun
				Noise Monitoring at NM2 & NM6		
11-Jun	12-Jun	13-Jun	14-Jun	15-Jun	16-Jun	17-Jun
			Noise Monitoring at NM2 & NM6			
18-Jun	19-Jun	20-Jun	21-Jun	22-Jun	23-Jun	24-Jun
		Noise Monitoring at NM2 & NM6				
25-Jun	26-Jun	27-Jun	28-Jun	29-Jun	30-Jun	
	Noise Monitoring at NM2 & NM6				Noise Monitoring at NM2 & NM6	

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - July 2017

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						01-Jul
02-Jul	03-Jul	04-Jul	05-Jul	06-Jul	07-Jul	08-Jul
				Noise Monitoring at NM2 & NM6		
09-Jul	10-Jul	11-Jul	12-Jul	13-Jul	14-Jul	15-Jul
			Noise Monitoring at NM2 & NM6			
16-Jul	17-Jul	18-Jul	19-Jul	20-Jul	21-Jul	22-Jul
		Noise Monitoring at NM2 & NM6				
23-Jul	24-Jul	25-Jul	26-Jul	27-Jul	28-Jul	29-Jul
	Noise Monitoring at NM2 & NM6				Noise Monitoring at NM2 & NM6	
30-Jul	31-Jul					

Annex E

Calibration Reports for Calibrators and Sound Level Meters



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

1

C166691

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC16-2717) Date of Receipt / 收件日期: 28 November 2016

Description / 儀器名稱

Acoustic Calibrator

Manufacturer / 製造商

Casella

Model No. / 型號

CEL-120/1 3421612

Serial No. / 編號 Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

30 November 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By 測試

HT Wong Technical Officer

Certified By

核證

Date of Issue 簽發日期

Website/網址: www.suncreation.com

7 December 2016

Project Engineer

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C166691

S,

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID CL130 CL281 TST150A <u>Description</u>

Universal Counter
Multifunction Acoustic Calibrator
Measuring Amplifier

Certificate No.

C163709 PA160023 C161175

4. Test procedure: MA100N.

5. Results:

5.1 Sound Level Accuracy

Journa Dever Treeding			
UUT	Measured Value	Mfr's Spec.	Uncertainty of Measured Value
Nominal Value	(dB)	(dB)	(dB)
94 dB, 1 kHz	94.1	± 0.25	± 0.2
114 dB, 1 kHz	114.1		

5.2 Frequency Accuracy

requested reconstant			
UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	1.000 0	$1 \text{ kHz} \pm 5 \text{ Hz}$	± 0.1

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C166692

S,

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC16-2717) Date of Receipt / 收件日期: 28 November 2016

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Casella

Model No. / 型號 Serial No./編號

CEL-633A 3521757

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}$ C Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

30 November 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By

測試

H T Wong

Technical Officer

Certified By

核證

K C Lee Project Engineer Date of Issue

7 December 2016

簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Page 1 of 4



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C166692

證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration using the Casella Acoustic Calibrator CEL-120/1, S/N: 3421612 was performed before the test.
- 3. The results presented are the mean of 3 measurement at each calibration point.
- 4. Test equipment:

Equipment ID CL280

Description

Certificate No.

CL281

40 MHz Arbitrary Waveform Generator Multifunction Acoustic Calibrator

C160077 PA160023

- 5. Test procedure: MA101N.
- 6. Results:
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

UUT	Setting	Applie	ed Value	UUT	IEC 61672 Class 1
Time	Frequency	Level	Freq.	Reading	Spec.
Weighting	Weighting	(dB)	(kHz)	(dB)	- (dB)
L_{F}	A	114.00	1	113.7	± 1.1

Linearity

UUT	Setting	Applie	Applied Value		
Time Frequency Weighting Weighting		Level (dB)	Freq. (kHz)	Reading (dB)	
L_{F}	A	114.00	1	113.7 (Ref.)	
		104.00		103.7	
		94.00		93.5	

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

UUT	Setting	Applied Value		UUT	IEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq. (kHz)	Reading (dB)	Spec. (dB)
L _F	A	114.00	1	113.7	Ref.
Ls				113.7	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C166692

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT	Setting	App	lied Value	UUT	IEC 61672 Class 1
Time	Frequency	Level	Freq.	Reading	Spec.
Weighting	Weighting	(dB)		(dB)	(dB)
L_{F}	A	94.00	63 Hz	87.4	-26.2 ± 1.5
			125 Hz	97.5	-16.1 ± 1.5
			250 Hz	105.0	-8.6 ± 1.4
			500 Hz	110.4	-3.2 ± 1.4
			1 kHz	113.7	Ref.
			2 kHz	114.9	$+1.2 \pm 1.6$
			4 kHz	114.6	$+1.0 \pm 1.6$
			8 kHz	112.2	-1.1(+2.1; -3.1)
			12.5 kHz	108.1	-4.3(+3.0; -6.0)

6.3.2 C-Weighting

UUT	Setting	Applied Value		UUT	IEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq.	Reading (dB)	Spec. (dB)
$L_{\rm F}$	C	94.00	63 Hz	112.8	-0.8 ± 1.5
			125 Hz	113.5	-0.2 ± 1.0
			250 Hz	113.7	0.0 ± 1.0
			500 Hz	113.7	0.0 ± 1.0
			1 kHz	113.7	Ref.
			2 kHz	113.5	-0.2 ± 1.0
			4 kHz	112.8	-0.8 ± 1.0
			8 kHz	110.4	-3.0 (+1.5; -3.0)
			12.5 kHz	106.2	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C166692

證書編號

Remarks: - UUT Microphone Model No.: CEL-251 & S/N: 1950

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 114 dB : 63 Hz - 125 Hz : \pm 0.45 dB

250 Hz - 500 Hz : $\pm 0.40 \text{ dB}$ 1 kHz : $\pm 0.30 \text{ dB}$ 2 kHz - 4 kHz : $\pm 0.45 \text{ dB}$ 8 kHz : $\pm 0.55 \text{ dB}$ 12.5 kHz : $\pm 0.80 \text{ dB}$

 $104 dB : 1 kHz : \pm 0.10 dB (Ref. 114 dB)$

94 dB : 1 kHz : \pm 0.10 dB (Ref. 114 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

Annex F

Event / Action Plans for Noise

Annex F Event and Action Plan for Noise

Event	Action								
	Environmental Team (ET)		dependent Environmental tecker (IEC)	A	uthorised Person (AP)	C	ontractor		
Action Level	 Notify IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, AP and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness. 	3.	Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the AP accordingly; Supervise the implementation of remedial measures.	 2. 3. 4. 	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to proposed remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented.	1.	Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.		
Limit Level	 Identify source; Inform IEC and AP; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, AP and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and AP informed of the results; If exceedance stops, cease additional monitoring. 	2.	Discuss amongst AP, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the AP accordingly; Supervise the implementation of remedial measures.	 1. 2. 3. 4. 5. 	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	 1. 2. 3. 4. 5. 	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the AP until the exceedance is abated.		

Annex G

Summary of Implementation Status

Annex G Implementation Schedule for Environmental Protection Measures (1 to 31 May 2017)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultur	al Heritag	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	
S3.9.2	S3.3.1	Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	√
S3.9.2	S3.3.3	Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement—of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies—related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	<>

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S3.7.1 & 3.7.2		checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built	Whole site	During detailed design,	west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4. √- CMP was implemented during the reporting month. There were no updates for the CMP.
		heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the cross referenced location plans and photo records. One set of updated CMP shall be submitted to the AMO for approval before the operation stage of the project.		construction, post- construction and operation	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status					
Landsca	Landscape & Visual									
S4.7.27	-	In-situ Tree Protection - Cordon Zone (CZ)	Whole site	During construction	<>					
		Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.								
S4.7.2	-	In-situ Tree Protection - Advanced & Phased Root Pruning	Whole site	During construction	N/A – no root pruning has been conducted yet					
		All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.								
S4.7.2	-	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the tree or at a suitable location on an adjacent building to provide the	Whole site	During construction	√					

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			
S4.7.2	S4	In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.	Whole site	During construction	✓
S4.7.2	-	Light Control Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	√ ·
S4.7.2	S4	Compensatory Tree Planting A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil underneath so that fertilizers and conditioners could be added on a	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	N/A - Compensatory Tree Planting will be conducted at later stage.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation. Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.			
S4.7.2	S4	Existing Granite Revetment Wall The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.	Inner Southern Wall	During detailed design and construction	√ ·
S4.7.2	-	New Custom Paving New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A – No custom paving was conducted during the reporting month.
S4.7.2	54	In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 - Tree Group Inspection Form and Form 2 - Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction.	Whole site	During post construction and operation	N/A - The quarterly inspection will be conducted at later stage.
Noise	1	1 *	1	I	
S5.9	-	The following site practices should be followed during the construction of the Project:	Whole Site	During	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		 Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 		construction	
S5.9	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	√ ·
S5.9	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.	Whole Site	During construction	√
S5.9	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	√
S5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	√
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures	Whole Site	During construction	√ ·

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		are properly implemented during the construction stage.			
Air Qu	ality				
S6.8.1	-	Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	V
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	√
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	V
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	V
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	√
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	V
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	V
S6.8.1	-	Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	V
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	<>
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if required, from the ground floor level of building for construction of superstructure of the new buildings.	Whole Site	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	√
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	V
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	$\sqrt{}$
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	√
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A - Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	√
Water (Quality			<u> </u>	
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A - Not observed.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	√ ·
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A - Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	√
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	<>

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	√ ·
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	\checkmark
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A - Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A - Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	√ ·
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	√
	Manageme		T	T	
S8.5	\$6.3.1 & Table 6.1	<u>General</u> The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	√
S8.5	-	Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	√
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket	Whole Site	During construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		system will be included as one of the contractual requirements and implemented by the contractor.			
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	√
S8.5	S6.3	Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	√
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	V
S8.5	S6	 Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. 	Whole Site	During construction and operation	√
S8.5	S6	 Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and 	Whole Site	During construction and operation	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		Be arranged so that incompatible materials are appropriately separated.			
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	√
S8.5	S6 & Table 6.1	General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	√
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	\checkmark
S8.5	S6	Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	√
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	√

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex G Implementation Schedule for Environmental Protection Measures (1 to 30 June 2017)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultura	al Heritag	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	√
S3.9.2	S3.3.1	Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	√
53.9.2	S3.3.3	Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	<>

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S3.7.1 & 3.7.2		checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built	Whole site	During detailed design,	west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4. √- CMP was implemented during the reporting month. There were no updates for the CMP.
		heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the cross referenced location plans and photo records. One set of updated CMP shall be submitted to the AMO for approval before the operation stage of the project.		construction, post- construction and operation	

EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status			
Landscape & Visual							
	<u>In-situ Tree Protection - Cordon Zone (CZ)</u>	Whole site	During construction	✓			
	Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.						
	In-situ Tree Protection - Advanced & Phased Root Pruning	Whole site	During construction	N/A – no root pruning has been conducted yet			
	All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.						
	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the	Whole site	During construction				
		pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree. In-situ Tree Protection - Foliage cleansing system	pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree. In-situ Tree Protection - Foliage cleansing system Whole site	pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree. In-situ Tree Protection - Foliage cleansing system			

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			
S4.7.2	S4	In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.	Whole site	During construction	✓
S4.7.2	-	Light Control Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	√ ·
S4.7.2	S4	Compensatory Tree Planting A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil underneath so that fertilizers and conditioners could be added on a	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	N/A - Compensatory Tree Planting will be conducted at later stage.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation. Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.			
S4.7.2	S4	Existing Granite Revetment Wall The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.	Inner Southern Wall	During detailed design and construction	√
S4.7.2	-	New Custom Paving New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A – No custom paving was conducted during the reporting month.
S4.7.2	54	In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 - Tree Group Inspection Form and Form 2 - Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction.	Whole site	During post construction and operation	N/A - The quarterly inspection will be conducted at later stage.
Noise	1	1 *	1	I	
S5.9	-	The following site practices should be followed during the construction of the Project:	Whole Site	During	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		 Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 		construction	
S5.9	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	√ ·
S5.9	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps.	Whole Site	During construction	√
S5.9	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	√
S5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	√
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures	Whole Site	During construction	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		are properly implemented during the construction stage.			
Air Qu	ality				
S6.8.1	-	Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	V
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	V
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	V
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	√
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	√
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	V
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	V
S6.8.1	-	Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	V
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	V
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if required, from the ground floor level of building for construction of superstructure of the new buildings.	Whole Site	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	√
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	V
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	$\sqrt{}$
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	√
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A - Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	√
Water (Quality			<u> </u>	
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A - Not observed.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	√
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A - Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	\checkmark
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	√ ·
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	\checkmark
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A - Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A - Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	√ ·
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	√
	Manageme		T	T	
S8.5	\$6.3.1 & Table 6.1	<u>General</u> The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	√
S8.5	-	Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	√
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket	Whole Site	During construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		system will be included as one of the contractual requirements and implemented by the contractor.			
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	√
S8.5	S6.3	Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	√
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	V
S8.5	S6	 Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. 	Whole Site	During construction and operation	√
S8.5	S6	 Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and 	Whole Site	During construction and operation	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		Be arranged so that incompatible materials are appropriately separated.			
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	√
S8.5	S6 & Table 6.1	General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	√
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	\checkmark
S8.5	S6	Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	√
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	√

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex G Implementation Schedule for Environmental Protection Measures (1 to 31 July 2017)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultur	al Heritag	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	V
S3.9.2	S3.3.1	Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	
S3.9.2	S3.3.3	Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement—of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies—related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S3.7.1 & 3.7.2		checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built	Whole site	During detailed design,	west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4. √- CMP was implemented during the reporting month. There were no updates for the CMP.
		heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the cross referenced location plans and photo records. One set of updated CMP shall be submitted to the AMO for approval before the operation stage of the project.		construction, post- construction and operation	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Landsca	ipe & Visu	ıal		•	
S4.7.27	-	Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.	Whole site	During construction	The chain-link fencing for the retained trees has been removed to enable the laying of floor slab and repairing of the planters. A tree protection zone around the planter of each tree has been provided. Barricades are set up for Tree 6, 7, 8 and 9 and the barricaded zone is clear of construction materials or equipment. The vicinity of Tree 5 is also clear of construction materials or equipment. A temporary shelter has been erected around Tree 11. No major construction works in the vicinity of the trees or within the CPS site are being carried out.
S4.7.2		All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.	Whole site	During construction	N/A – no root pruning has been conducted yet
S4.7.2	-	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the	Whole site	During construction	N/A - The sprinkler cleansing system has been removed as major dust-generating works within the

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		tree or at a suitable location on an adjacent building to provide the means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			CPS site have been completed.
S4.7.2	S4	In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.	Whole site	During construction	✓
S4.7.2	-	Light Control Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	✓
S4.7.2	S4	Compensatory Tree Planting A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	√ - Planters of the compensatory trees are being built in the Parade Ground during the reporting period.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.			
		Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements			
		The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.			
S4.7.2	S4	Existing Granite Revetment Wall The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.	Inner Southern Wall	During detailed design and construction	✓
S4.7.2	-	New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A - No custom paving was conducted during the reporting month.
S4.7.2	S4	In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 - Tree Group Inspection Form and Form 2 - Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction.	Whole site	During post construction and operation	N/A - The quarterly inspection will be conducted at later stage.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S5.9	-	 The following site practices should be followed during the construction of the Project: Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 	Whole Site	During construction	
S5.9	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	
S5.9 S5.9	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps. Use quiet PME as far as practicable to mitigate the construction noise	Whole Site Whole Site	During construction During	√ √
		impact.		construction	
S5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	\bigvee

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	√ ·
Air Qua	ality				
S6.8.1	-	Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	√
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	√ ·
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	√ ·
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	√
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	√
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	√ ·
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	√ ·
S6.8.1	-	Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	√
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	√
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if	Whole Site	During	√

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		required, from the ground floor level of building for construction of superstructure of the new buildings.		construction	
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	√
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	√ ·
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	√ ·
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	√
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A - Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	√ ·
Water (Quality				
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A - Not observed.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	√
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A - Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A - Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	\checkmark
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	V

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	√ ·
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	\checkmark
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A - Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A - Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	√ ·
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	√
	Manageme		T	T	
S8.5	\$6.3.1 & Table 6.1	<u>General</u> The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	√
S8.5	-	Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	√
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket	Whole Site	During construction	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		system will be included as one of the contractual requirements and implemented by the contractor.			
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	√
S8.5	S6.3	Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	√
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	V
S8.5	S6	 Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. 	Whole Site	During construction and operation	√
S8.5	S6	 Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and 	Whole Site	During construction and operation	

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		Be arranged so that incompatible materials are appropriately separated.			
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	√
S8.5	S6 & Table 6.1	General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	√
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	\checkmark
S8.5	S6	Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	√
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	√

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex H

Noise Monitoring Results

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results

NM6 Chancery Mansion

Date	Start Time	End Time	Weather	Noise level (dB(A)), 30 min			Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90		Observed		()		
05-May-17	9:50	10:20	Sunny	66.6	69.5	63.7	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
11-May-17	9:44	10:14	Fine	66.7	68.2	63.4	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
17-May-17	9:07	9:37	Fine	67.5	70.7	63.6	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
23-May-17	9:20	9:50	Sunny	65.4	66.8	63.3	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
29-May-17	10:40	11:10	Sunny	64.3	65.9	62.6	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
							<u> </u>					

Min. 64.3 Max. 67.5

NM2 Ho Fook Building

	Ť			Noise	level (dB(A)), 30 min	Major Construction Noise Source(s) Observed	Other Noise		Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90		Source(s) Observed	Remarks	(m/s)	Model / ID	Model / ID
05-May-17	9:12	9:42	Sunny	68.4	71.7	64.8	Interior fitting (within the project site)	Traffic noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
11-May-17	10:22	10:52	Fine	68.3	69.9	63.9	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
17-May-17	9:45	10:15	Fine	70.6	73.8	66.7	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
23-May-17	10:00	10:30	Sunny	67.5	70.3	64.6	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
29-May-17	8:44	9:14	Sunny	69.2	71.4	65.4	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min	67.5								

Min. 67.5 Max. 70.6

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results

NM6 Chancery Mansion

Date	Start Time	End Time	Weather	Noise	level (dB(A)), 30 min	Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID	
				Leq	L10	L90		Observed		()			
02-Jun-17	9:10	9:40	Sunny	64.1	65.8	62.0	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
08-Jun-17	10:09	10:39	Sunny	65.0	66.1	63.7	Interior fitting (within the project site)	Traffic Noise	-	0.6	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
14-Jun-17	15:25	15:55	Cloudy	64.3	65.9	62.3	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
20-Jun-17	10:15	10:45	Cloudy	64.4	66.3	62.0	Interior fitting (within the project site)	Traffic Noise	-	0.4	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
26-Jun-17	9:38	10:08	Sunny	66.7	69.3	64.2	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
30-Jun-17	8:42	9:12	Sunny	62.7	65.0	61.3	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
			Min.	62.7									
			Max.	66.7									

NM2 Ho Fook Building

				Noise	level (dB(A)), 30 min	Major Construction Noise	Other Noise		Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Source(s) Observed	Source(s) Observed	Remarks	(m/s)	Model / ID	Model / ID
02-Jun-17	9:49	10:19	Sunny	69.5	72.1	65.7	Interior fitting (within the project site)	Traffic noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
08-Jun-17	10:48	11:18	Sunny	71.0	72.7	68.3	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
14-Jun-17	13:32	14:02	Cloudy	66.3	68.7	63.8	Interior fitting (within the project site)	Traffic Noise	-	0.4	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
20-Jun-17	10:55	11:25	Cloudy	68.8	71.4	65.2	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
26-Jun-17	10:18	10:48	Sunny	67.7	70.1	64.2	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
30-Jun-17	9:20	9:50	Sunny	67.1	69.1	64.1	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	66.3			<u> </u>					

Min. 66.3 Max. 71.0

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results


NM6 Chancery Mansion


Date	Start Time	End Time	Weather	Noise	level (dB(A))	, 30 min	Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90	(0)	Observed		()		
06-Jul-17	14:25	14:55	Cloudy	68.3	69.7	65.9	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
12-Jul-17	11:00	11:30	Sunny	64.4	65.7	62.2	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
18-Jul-17	13:03	13:33	Cloudy	65.2	66.8	63.5	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
24-Jul-17	8:47	9:17	Fine	63.4	64.8	61.5	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
28-Jul-17	8:20	8:50	Sunny	63.3	64.8	61.3	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	63.3								
			Max.	68.3								

NM2 Ho Fook Building

NWZ HO FOO				Noise	level (dB(A)), 30 min		Other Noise				
Date	Start Time	End Time	Weather	Leq	L10	L90	Major Construction Noise Source(s) Observed	Source(s) Observed	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
06-Jul-17	9:20	9:50	Cloudy	64.0	65.4	62.3	Interior fitting (within the project site)	Traffic noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
12-Jul-17	10:18	10:48	Sunny	65.9	67.5	63.1	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
18-Jul-17	13:40	14:10	Cloudy	67.5	69.5	63.2	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
24-Jul-17	9:25	9:55	Fine	64.8	66.4	62.2	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
28-Jul-17	10:15	10:45	Sunny	64.9	66.7	62.6	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	64.0								

Min. 64.0 Max. 67.5

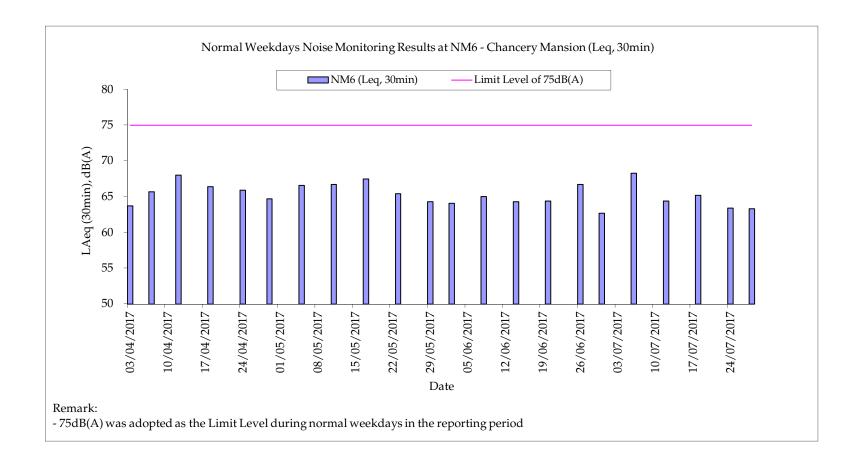

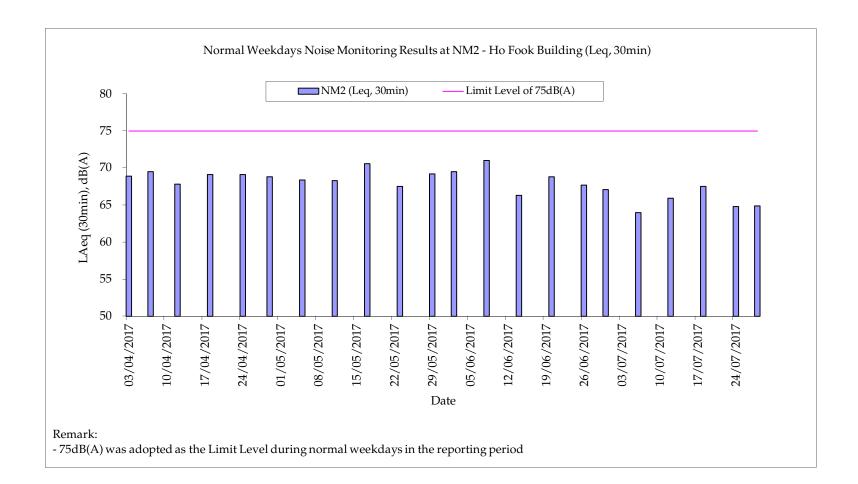


Annex I

Construction Programme for the Project

Activity	Activity	Orig Start	Finish	2017 2018
CENTRAL POLI	Description CE STATION	Dur Date	Date	M APR MAY JUN JUL AUG SEP OCT NOV DEC JAN FEB
	E HEADQUARTERS			
SB01-0010	BLOCK 1 - FACADE WORK	201* 21JUL16A	06FEB17A	
SB01-0010	BLOCK 1 - FINISHES & E/M INCL TEMP SITE OFFICE	384* 21JUL16A		
BLOCK 2 - ARMO		304 Z100E10A	OUNDOTT	
SB02-0010	BLOCK 2 - FACADE WORK	36* 21OCT16A	25NOV16A	
SB02-0020	BLOCK 2 - FINISHES & E/M WORK	245* 21JUL16A		
BLOCK 3 - BARRA		243 2100E10A	ZZIVIAITITA	
SB03-0010	BLOCK 3 - FACADE WORK	249* 21SEP16A	27MAY17	BLOCK 3 - FACADE WORK
SB03-0020	BLOCK 3 - FINISHES, E/M WORK & PART FLOOR STRAP	229* 05DEC16A	21JUL17	BLOCK 3 - FINISHES, E/M WORK & PART FLOOR STRAP
SB03-0030	BLOCK 3 - 2/F FLOOR STRAP	73* 05AUG17	16OCT17	BLOCK 3 - 2/F FLOOR STRAP(AFTER OP)
BLOCK 6 - DORM	I .	73 03A0017	1000117	
SB06-0010	BLOCK 6 - FACADE WORK	33* 01NOV16A	03DEC16A	
				BLOCK 6 - FINISHES & E/M WORK
	BLOCK 6 - FINISHES & E/M WORK	302* 09AUG16A	U6JUN17	SECONO-1 MIGRIES & EAM WORK
BLOCK 7 - DORM	T	200* 0041/0104	00 11 1014 7	BLOCK 7 - FINISHES & E/M WORK
SB07-0010	BLOCK 7 - FINISHES & E/M WORK	302* 09AUG16A	U6JUN17	SECONT - I MORIES & LIM WORK
BLOCK 8 - ABLUT		170* 04101464	0014147	BLOCK 8 - FACADE WORK
SB08-0010	BLOCK 8 - FACADE WORK	178* 24NOV16A		
	BLOCK 8 - FINISHES & E/M WORK	270* 07OCT16A	03JUL17	BLOCK 8 - FINISHES & E/M WORK
	RAL MAGISTRACY			BLOCK 9 - FACADE WORK INCL SOUTH ELEVATION
SB09-0010	BLOCK 9 - FACADE WORK INCL SOUTH ELEVATION	406* 25AUG16A		
SB09-0020	BLOCK 9 - FINISHES & E/M WORK	401* 25AUG16A		BLOCK 9 - FINISHES & E/M WORK
SB09-0030	BLK 9-COURT RM/ CANOPY STRENGTHEN &REINSTATEMENT	223* 26MAY17	03JAN18	BLK 9-COURT RM/ CANOPY STREM
BLOCK 10 - SUPE	RINTENDENTS HOUSE			
SB10-0010	BLOCK 10 - FACADE WORK INCL BALCONY REPAIR	398* 06OCT16A	07NOV17	BLOCK 10 - FACADE WORK INCL BALCONY REPAIR
SB10-0020	BLOCK 10 - FINISHES & E/M WORK INCL FLOOR STRAP	387* 04OCT16A	25OCT17	BLOCK 10 - FINISHES & E/M WORK INCL FLOOR STRAP
BLOCK 11 - A HAI	L		<u> </u>	
SB11-0010	BLOCK 11 - FACADE WORK	219* 07OCT16A	13MAY17	
SB11-0020	BLOCK 11 - FINISHES & E/M WORK	233* 24NOV16A	14JUL17	BLOCK 11 - FINISHES & E/M WORK
BLOCK 12 - B HA	LL.			
SB12-0010	BLOCK 12 - FACADE WORK	376* 14JUL16A	24JUL17	BLOCK 12 - FACADE WORK
SB12-0020	BLOCK 12 - FINISHES & E/M WORK	365* 14JUL16A	13JUL17	BLOCK 12 - FINISHES & E/M WORK
BLOCK 13 - C HA	LL			
SB13-0010	BLOCK 13 - FACADE WORK INCL CANOPY REMOVAL	257* 06OCT16A	19JUN17	BLOCK 13 - FACADE WORK INCL CANOPY REMOVAL
SB13-0020	BLOCK 13 - FINISHES & E/M WORK	262* 06OCT16A	24JUN17	BLOCK 13 - FINISHES & E/M WORK
BLOCK 14 - D HA	LL			
SB14-0010	BLOCK 14 - FACADE WORK	281* 21SEP16A	28JUN17	BLOCK 14 - FACADE WORK
SB14-0020	BLOCK 14 - FINISHES & E/M WORK INC CROSS BRACING	290* 21SEP16A	07JUL17	BLOCK 14 - FINISHES & E/M WORK INC CROSS BRACING
BLOCK 15 - E HAI	LL			
SB15-0010	BLOCK 15 - FACADE WORK	244* 04JUL16A	04MAR17A	
SB15-0020	BLOCK 15 - FINISHES & E/M WORK	356* 04JUL16A		BLOCK 15 - FINISHES & E/M WORK
BLOCK 17 - F HAI				
SB17-0010	BLOCK 17 - FACADE WORK INC EXT WINDOW TOP RAIL	310* 21JUL16A	26MAY17	BLOCK 17 - FACADE WORK INC EXT WINDOW TOP RAIL
SB17-0020	BLOCK 17 - FINISHES & E/M WORK	335* 21JUL16A		BLOCK 17 - FINISHES & E/M WORK
BLOCK 19 - BAUH		233 2.332.134		
	BLOCK 19 - FINISHES & E/M WORK	195* 11NOV16A	24MAY17	BLOCK 19 - FINISHES & E/M WORK
BLOCK 50 OLD B	I .	1.10 11110 1011	= 117	
SB50-0010	OBW FINISHES & E/M WORK INC R54	416* 20JUN16A	09AUG17	OBW FINISHES & E/M WORK INC R54
art Date nish Date	07JUL10 09AUG18	Early Bar	7D02	CENTRAL POLICE STATION Sheet 1 of 2 Date GCL/P/J3416/SUM/CP07B
ata Date	27APR17	Progress Bar		CONSERVATION AND REVITALIZATION
un Date	04MAY17 13:04		SI	SUMMARY PROGRAMME TO COMPLETION REV 7B (EXCL BLOCK 4) 6
				(EXCL BLOCK 4) Gammon Jockey Club
	l l		1	(WITH PROGRESS AS OF 27 APRIL 2017)

Activity ID	Activity Description	Orig Start Dur Date	Finish Date	405				2017	OFD	007	NOV	DE0.		2018	
BLOCK 51 ARBU	· · · · · · · · · · · · · · · · · · ·	Dui Duit	Dute	M APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MA
SB51-0010	AW - FINISHES & E/M WORK	379* 20JUN16	A 03JUL17			AV	W - FINISHES	& E/M WORK				 			1
EXTERNAL WOR	KS														1
SBEW-0010	EXTERNAL WORK (INCL BLK 4 PROTECTIVE PLATFORM)	543* 04JUL16	A 28DEC17		1						· · · · · · · · · · · · · · · · · · ·	<u>'</u>	EXTERNAL WOR	K (INCL BLK 4	PROTEC
STATUTORY INSI	PECT & HANDOVER (EXCL BLK 09 & 10)														
SBST-0010	SUBMIT BA13 & BA14	0	21JUL17				♦ SUE	MIT BA13 & BA1	4			1			1
SBST-0020	BD INSPECTION	14* 22JUL1	7 04AUG17					BD INSPECTIO	N						
SBST-0030	ISSUE OP & BA14 ACKNOWLEDGEMENT	0	04AUG17					♦ISSUE OP & B	BA14 ACKNOWL	EDGEMENT				1	
SBST-0040	HANDOVER FOR PC	27* 22JUL1	7 17AUG17					HANDO	VER FOR PC						
SBST-0050	PRACTICAL COMPLETION	0	17AUG17					◆PRACT	TICAL COMPLET	TION		 		1	1
STATUTORY INSI	PECTIONS & HANDOVER (BLK 10)		<u>'</u>					İ				 		 	
SBST-0170	SUBMIT BA14	0	03NOV17								SUBMIT BA	14		 	
SBST-0180	BD INSPECTION	28* 04NOV1	7 01DEC17		!							BD INSPECTIO	N	1	1
SBST-0190	ISSUE BA14 ACKNOWLEDGEMENT	0	01DEC17									♦ISSUE BA14 A	CKNOWLEDGE	WENT	
SBST-0200	HANDOVER FOR PC	28* 04NOV1	7 01DEC17									HANDOVER FO	R PC	1	1
SBST-0210	PRACTICAL COMPLETION	0	01DEC17					 				PRACTICAL C	OMPLETION	 	į
STATUTORY INSI	PECTIONS & HANDOVER (BLK 9)		·											i i	
SBST-0110	SUBMIT BA14	0	14DEC17									SUBMI	T BA14	İ	į
SBST-0120	BD INSPECTION	28* 15DEC1	7 11JAN18										BD INSPE	CTION	
SBST-0130	ISSUE BA14 ACKNOWLEDGEMENT	0	11JAN18								1	1	♦ISSUE B	A14 ACKNOW	LEDGEME
SBST-0140	HANDOVER FOR PC	28* 15DEC1	7 11JAN18										HANDOVI	R FOR PC	
SBST-0150	PRACTICAL COMPLETION	0	11JAN18								1	1	◆PRACTION	CAL COMPLET	ION



CENTRAL POLICE STATION
CONSERVATION AND REVITALIZATION


SUMMARY PROGRAMME TO COMPLETION REV 7B (EXCL BLOCK 4)

(WITH PROGRESS AS OF 27 APRIL 2017)



Sheet 2 of 2

	GCL/P/J3416/SUM/CP07B											
Date	Revision	Checked	Approved									

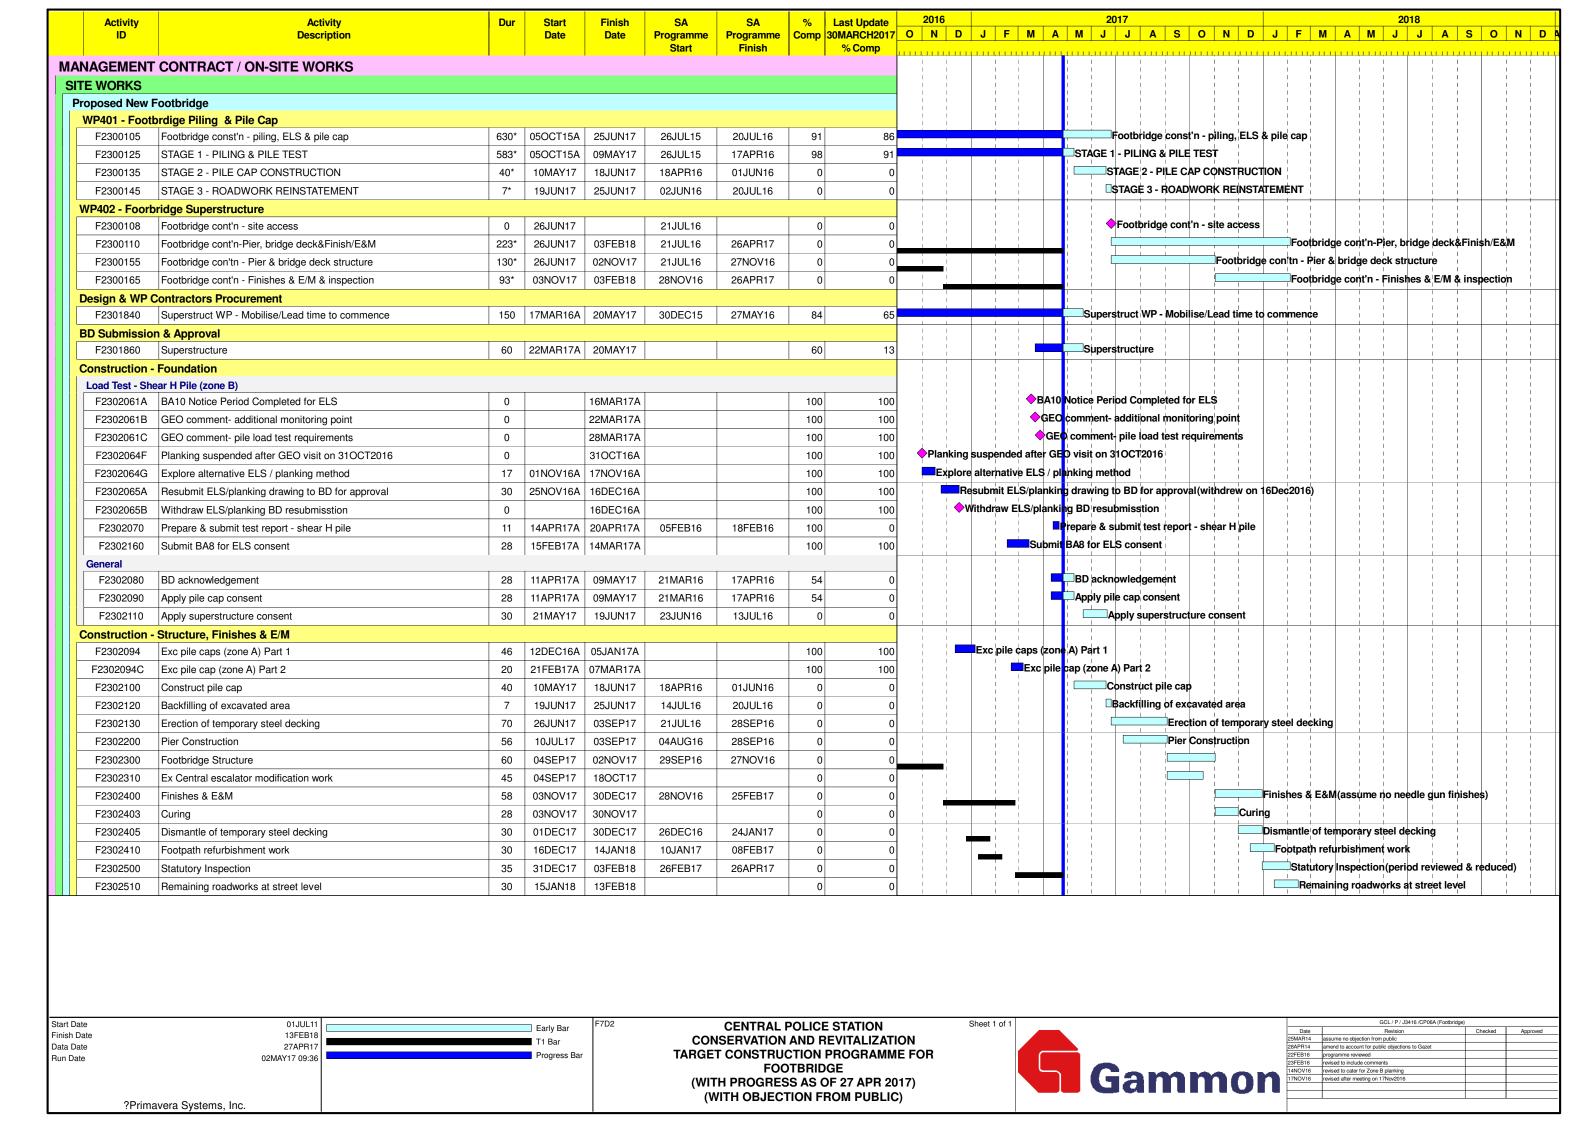

Annex J

Waste Flow Table

Annex J - Waste Flow Table

Month / Year			** 1 (6:-	CARAL		iantity	GI . I				
	C&D Materials (inert) (tonnes) (a)	Number of Trucks for C&D Materials	Volume of C&D Materials (inert)	(non-inert)	Number of Trucks for C&D Materials	Materials (non-	Waste (Solid	Chemical Waste	Recycled materials		
		Disposal (inert)	(m ³) (c)	(tonnes) (b)	Disposal (non-inert)	inert) (m ³) (c)	/kg)	(Liquid/L)	Paper/cardboard (kg)	Plastics (kg)	Metals (k
October 2011 –											
lovember 2011	0	0	0	33.5	12	58.50	0	0	38	6	36423
ecember-11	0	0	0	18.25	6	29.25	0	0	112	0	24000
nuary-12	354.14	40	195.00	16.88	5	24.38	2400	0	0	0	3820
ebruary-12	252.35	15	73.13	17.13	5	24.38	1400	0	223	0	8910
Iarch-12	666.43	62	302.25	28.56	9	43.88	3200	0	0	0	48490
pril-12	688.68	72	351.00	17.54	5	24.38	0	0	0	0	12403
1ay-12	492.33	61	297.38	36.33	13	63.38	0	0	266	0	0
ine-12	383.11	45	219.38	27.41	8	39.00	40	45	0	0	1100
uly-12	217.98	25	121.88	23.22	8	39.00	0	0	302	0	1750
ugust-12	341.87	42	204.75	48.87	16	78.00	0	0	0	0	2310
eptember-12	227.7	29	141.38	37.99	12	58.50	0	0	383	0	1410
October-12	290.58	44	214.50	30.34	8	39.00	0	0	86	0	3150
lovember-12	843.86	100	487.50	47.44	15	73.13	0	0	0	0	5650
ecember-12	207.5	27	131.63	88.66	28	136.50	0	0	0	0	27230
anuary-13	273.64	34	165.75	276.17	74	360.75	0	0	172	0	8120
ebruary-13	945.97	131	638.63	177.54	46	224.25	0	0	0	0	1080
Iarch-13	1236.96	151	736.13	230.55	60	292.50	0	0	164	0	11300
pril-13	1406.79	187	911.63	232.27	63	307.13	135	12	225	0	21220
Iay-13	2679.91	317	1545.38	176.68	44	214.50	0	0	62	0	17286
ine-13	3062.38	356	1735.50	212.63	56	273.00	0	0	0	0	7150
ıly-13	3814.86	465	2266.88	114.36	43	209.63	0	0	168	0	14843
ugust-13	2831.78	353	1720.88	89.23	25	121.88	0	0	0	0	7190
eptember-13	979.49	141	687.38	103.73	29	141.38	40	0	0	0	4030
ctober-13	2170.54	270	1316.25	157.48	41	199.88	135	0	0	0	3120
lovember-13	836.74	109	531.38	191.58	44	214.50	0	0	202	0	1848
ecember-13	2606.76	296	1443.00	192.54	49	238.88	0	0	0	0	1004
nuary-14	3813.53	400	1950.00	97.87	36	175.50	0	0	0	0	1411
bruary-14	3378.16	316	1540.50	37.84	14	68.25	0	0	0	0	9800
larch-14	5256.15	516	2515.50	89.39	31	151.13	0	0	6000	0	19030
pril-14	3006	299	1457.63	114.31	33	160.88	45	0	0	0	6950
lay-14	3195.53	310	1511.25	119.54	37	180.38	0	0	0	0	7000
ine-14	2176.81	205	999.38	148.8	45	219.38	0	0	242	0	8830
ly-14	1009.96	111	541.13	147.36	49	238.88	0	0	0	0	6680
ugust-14	379.23	53	258.38	211.86	47	229.13	0	0	0	0	1369
eptember-14	1216.97	123	599.63	264.83	56	273.00	0	0	0	0	9720
ctober-14	1162.34	124	604.50	294.33	65	316.88	0	0	0	0	57080
lovember-14	1249.55	141	687.38	336.57	75	365.63	0	0	0	0	6660
ecember-14	1177.63	129	628.88	260.33	69	336.38	0	0	68	0	12080
nuary-15	614.34	69	336.38	222.32	58	282.75	0	0	0	0	3000
ebruary-15	593.97	78	380.25	133.74	40	195.00	0	0	0	0	5420
farch-15	766.35	93	453.38	245.77	40 71		0	0	106	0	8980
		78			51	346.13	0	0	0	0	
pril-15	594.77 832.50	110	380.25 536.25	195.55 212.04	63	248.63	0	0	133	0	3370 5090
lay-15						307.13					
ine-15	673.87	84	409.50	222.66	72	351.00	0	0	23	0	0
ıly-15	1133.90	137	667.88	184.02	62	302.25	0	0	0	0	6950
ugust-15	1394.20	157	765.38	226.04	81	394.88	0	0	0	0	0
ptember-15	942.39	107	521.63	330.23	108	526.50	0	0	0	0	0
ctober-15	1874.26	220	1072.50	286.27	109	531.38	0	0	60	0	0
ovember-15	830.67	93	453.38	321.6	117	570.38	0	0	86	0	4970
ecember-15	596.00	58	282.75	250.51	107	521.63	0	0	103	0	1677
nuary-16	505.11	57	277.88	265.56	120	585.00	0	0	0	0	6340
bruary-16	274.16	30	146.25	128.66	70	341.25	0	0	170	0	0
larch-16	114.67	17	82.88	380.06	116	565.50	0	0	0	0	0
pril-16	244.83	34	165.75	308.28	113	550.88	0	0	0	0	0
ay-16	402.49	55	268.13	216.79	74	360.75	0	0	0	0	0
ne-16	173.01	20	97.50	109.25	36	175.50	0	0	248	0	0
ly-16	303.68	37	180.38	83.99	40	195.00	0	0	0	0	0
ıgust-16	147.28	19	92.63	112.63	46	224.25	0	0	0	0	0
ptember-16	17.64	3	14.63	88.26	39	190.13	0	0	226	0	0
ctober-16	57.59	9	43.88	69.64	28	136.50	0	0	0	0	0
ovember-16	14.21	2	9.75	105.39	33	160.88	0	0	0	0	0
ecember-16	29.61	4	19.50	69.45	27	131.63	0	0	260	0	0
nuary-17	27.51	4	19.50	51.97	22	107.25	0	0	190	0	0
bruary-17	60.97	9	43.88	43.89	15	73.13	0	0	210	0	0
arch-17	135.47	17	82.88	93.05	27	131.63	0	0	160	0	0
oril-17	32.19	4	19.50	103.21	28	136.50	0	0	0	0	0
		8	39.00	87.19			0	0	0	0	0
ay-17	54.34 134.59	8 15	73.13	87.19 80.65	26 30	126.75 146.25	0	0		0	
a. 17		15	7.5.13	80.65		146.25		()	0	0	0
ne-17 ly-17	12.61	1	4.88	57.54	24	117.00	0	0	0	0	0

Notes:

(a) Inert C&D materials (public fill) include bricks, concrete, building debris, rubble and excavated soil.

⁽b) Non-inert C&D materials include wastes such as generall refuse and mixed construction waste.

⁽c) If necessary, use the conversion factor: 3/4 load of dumping truck being equivalent to $6.5~\text{m}^3$ by volume.

Annex K

Environmental Complaint, Environmental Summons and Prosecution Log

Annex K Cumulative Complaint and Summons/Prosecutions Log

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	4	0
April 2012	0	0
May 2012	0	0
June 2012	2	0
July 2012	1	0
August 2012	0	0
September 2012	0	0
October 2012	0	0
November 2012	2	0
December 2012	0	0
January 2013	0	0
February 2013	1	0
March 2013	1	0
April 2013	0	0

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
May 2013	0	0
June 2013	0	0
July 2013	0	0
August 2013	0	0
September 2013	0	0
October 2013	0	0
November 2013	0	0
December 2013	0	0
January 2014	2	0
February 2014	1	0
March 2014	1	0
April 2014	1	0
May 2014	0	0
June 2014	0	0
July 2014	2	0
August 2014	3	0
September 2014	2	0
October 2014	1	0
November 2014	0	0

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2014	0	0
January 2015	0	0
February 2015	1	0
March 2015	1	0
April 2015	0	0
May 2015	1	0
June 2015	1	0
July 2015	1	0
August 2015	1	0
September 2015	0	0
October 2015	0	0
November 2015	0	0
December 2015	0	0
January 2016	0	0
February 2016	0	0
March 2016	1	0
April 2016	0	0
May 2016	0	0
June 2016	0	0

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
July 2016	0	0
August 2016	0	0
September 2016	1	0
October 2016	0	0
November 2016	0	0
December 2016	0	0
January 2017	0	0
February 2017	0	0
March 2017	0	0
April 2017	0	0
May 2017	0	0
June 2017	0	0
July 2017	0	0
Overall Total	32	0

Annex L

Records of Vibration Monitoring for Other Construction Works

Structural Additions and Alterations at Block 11 WYNDHAM \$ STREET 22-3/3066/10/BLK11 (HU) (S) F.S.D. Ref No. 消防療機築編號 11SW-B/R18 11SW-B/R17 Shiu King The Centrium Gourt - 11SW-B/R806 11SW-B/R23-11SW-B/R52 GS12 - 11SW-B/R24 BS14-17 CHIONG Kam-yueng lacky Chief Structural Engineer for BUILDING AUTHORITY BS13-3 - 3 OCT 2612 ₩15-2 11SW-B/R53 11SW-B/R176 **Д**VM15−1 BS3-5/ BT3-3 11SW-B/R19 BS1-14/ BT1-7 11SW-8/R174 ₩BS14-6 DH21(S,P) BD SUBMISSION 11SW-B/R175-Drawing Status 製圖狀況 GS20 retevant consultants。 未經有關解問公司書而同意。不包裝製此區級內任何 次交替1954 LEGEND Do not take measurements directly from 切勿直沒從雪紙上豐度尺寸。 Check and verify all dimensions on site 符有尺寸必須在工地現場按查及審核 EXISTING FRESH WATER MAIN Read this drawing in conjunction with the specification and all other related drawings.
 此匯纸必須與根格投明實及其它有關團級一併閱讀。 IN50-2 -3 — ADH4(S/P) EXISTING STREET LIGHTING NC. 33488-A1 discrepancy found herein, 如發現內容存任何朦朧之處。應立刻通知初聲明問公元 BS2-3 BS3-2/ 11SW-B/R19 EXISTING STREET LIGHTING CABLE 11SW-B/R177 -11SW-B/R55 EXISTING HV ELECTRICITY CABLE EXISTING IN FLECTRICITY CARLE HERZOG & DEMEURON EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED)
EXISTING STORMWATER DRAIN EXISTING FOUL SEWER ROCCO PROPOSED FOUL SEWER Structural Engineer / RSE E & M Engineer JRP ARUP EXISTING RETAINING WALL Project ঘটি CENTRAL POLICE STATION CONSERVATION AND REVITALISATION PROJECT DH1(S,P) 11SW-B/R54 EXISTING DRILLHOLE WITH BS17-13 - 11SW-B/R178 STANDPIPE/PIEZONETER Drawing Title 劉名 BS1-1/BT1-1 MONITORING LAYOUT PLAN RS174-1/RT174-1 PROPOSED RETAINING WALL SETTLEMENT POINTS/TILTMETER PROPOSED INCLINOMETER TO BE BUILT IN BORED PILE WALL OR PIPE PILE WALL 1:300名1 K.C.Lai AL Revision博改版 00-0AP209674-G-001 M PROPOSED GROUND SETTLEMENT POINTS U∏1 ⊠ PROPOSED UTILITY MONITORING POINTS PROPOSED VIBRATION MONITORING POINTS ADH1(S/P) PROPOSED ADDITIONAL DRILLHOLE Cod Re : 00-0AP2095/4-G-001.deg

Vibration Monitoring Record (May)

	Bloc	k 11
Point	VM11-1	VM11-2
Date	mm/s	mm/s
1-May-17	Hol	iday
2-May-17	0.100	0.109
3-May-17	Hol	iday
4-May-17	0.094	0.104
5-May-17	0.100	0.102
6-May-17	0.099	0.103
7-May-17	Sun	ıday
8-May-17	0.090	0.105
9-May-17	0.100	0.102
10-May-17	0.102	0.107
11-May-17	0.086	0.102
12-May-17	0.106	0.100
13-May-17	0.102	0.109
14-May-17	Sun	ıday
15-May-17	0.099	0.095
16-May-17	0.103	0.108
17-May-17	0.109	0.111
18-May-17	0.102	0.105
19-May-17	0.090	0.105
20-May-17	0.086	0.102
21-May-17	Sun	ıday
22-May-17	0.084	0.104
23-May-17	0.109	0.105
24-May-17	0.102	0.110
25-May-17	0.100	0.104
26-May-17	0.094	0.102
27-May-17	0.085	0.109
28-May-17	Sun	nday
29-May-17	0.097	0.115
30-May-17	Hol	iday
31-May-17	0.083	0.107

Vibration Monitoring Record (June 2017)

	Bloc	k 11
Point	VM11-1	VM11-2
Date	mm/s	mm/s
01-Jun-17	0.076	0.108
02-Jun-17	0.076	0.108
03-Jun-17	0.076	0.108
04-Jun-17	Sun	ıday
05-Jun-17	0.105	0.103
06-Jun-17	0.109	0.105
07-Jun-17	0.102	0.094
08-Jun-17	0.100	0.100
09-Jun-17	0.109	0.108
10-Jun-17	0.105	0.109
11-Jun-17	Sun	ıday
12-Jun-17	0.117	0.102
13-Jun-17	0.107	0.099
14-Jun-17	0.102	0.092
15-Jun-17	0.105	0.106
16-Jun-17	0.105	0.103
17-Jun-17	0.102	0.106
18-Jun-17	Sun	ıday
19-Jun-17	0.105	0.107
20-Jun-17	0.109	0.102
21-Jun-17	0.102	0.110
22-Jun-17	0.109	0.108
23-Jun-17	0.105	0.100
24-Jun-17	0.109	0.101
25-Jun-17	Sun	nday
26-Jun-17	0.105	0.093
27-Jun-17	0.101	0.100
28-Jun-17	0.110	0.100
29-Jun-17	0.106	0.104
30-Jun-17	0.117	0.109

Vibration Monitoring Record (July)

	Bloc	ck 11
Point	VM11-1	VM11-2
Date	mm/s	mm/s
01-Jul-17	Hol	iday
02-Jul-17	Sur	nday
03-Jul-17	0.105	0.104
04-Jul-17	0.103	0.110
05-Jul-17	0.114	0.100
06-Jul-17	0.109	0.109
07-Jul-17	0.122	0.102
08-Jul-17	0.107	0.105
09-Jul-17	Sur	nday
10-Jul-17	0.108	0.101
11-Jul-17	0.107	0.105
12-Jul-17	0.125	0.105
13-Jul-17	0.105	0.100
14-Jul-17	0.108	0.103
15-Jul-17	0.102	0.105
16-Jul-17	Sur	nday
17-Jul-17	0.105	0.102
18-Jul-17	0.109	0.103
19-Jul-17	0.102	0.107
20-Jul-17	0.118	0.102
21-Jul-17	0.105	0.105
22-Jul-17	0.109	0.117
23-Jul-17	Sur	nday
24-Jul-17	0.110	0.102
25-Jul-17	0.128	0.107
26-Jul-17	0.129	0.105
27-Jul-17	0.105	0.108
28-Jul-17	0.112	0.110
29-Jul-17	0.110	0.105
30-Jul-17	Sur	nday
31-Jul-17	0.114	0.107

Annex M

Non-compliance Reports and Summary of Condition of Character Defining Elements, Historic Buildings and Structures

Annex M1

Non-compliance Reports



This Site Memorandum confirms a variation of the Works following oral instructions, an inspection of site operations or the issuance of new or revised documents for construction. Unless stated otherwise, it shall be treated as an Instruction to carry out works as authorised by Architects Instruction F-620 dated 12 March 2014. Where applicable, it includes provision for distribution to all relevant members of the client/design/construction team and the Antiquities and Monuments Office.

Site Memorandum No. 1053

Date: 18th May 2017

To: Gammon Construction Limited For the attention of: Cliff Leung

Subject: Non-compliance, Loss of Gate/Fence "A" in A Hall

A.I. no: F-620

JCCPS

It was reported by the Management Contractor on 13th March 2017 that Gate/Fence "A" located within A Hall Yard has been lost. (Refer to plan overleaf for location and photograph.)

The Management Contractor and Works Package Contractors are required to:

- 1. Review and revise the work practices of handling and storing historic building fabric.
- Supervise the work operations to ensure compliance with the Contract Documents and submit mitigation measures to enhance precautionary and storage measures.
- 3. Fabricate new metal gate/fence to match the original as per design detailed on Site Memo 1029.

(Continue over leaf)

Heritage Impact: Historic fabric has been lost.

Proposed Mitigation Measures: Instruct Contractor to comply with Contract Documents. Fabricate new metal gate to match original.

LB Cost estimate:

Justification: N/A

Variation: N

Cost implication: N			HKD Initials: Date:			roved/rejected als: e:
Copies	to:					
٧	Employer JCCPS	٧	Structural Eng	Arup		
1	Quantity Surveyor RLB	٧	Services Eng	JRP	V	Environmental Management ERM
1	Contract Administrator RDA	V	Design Consultant	HdM	V	Antiquities & Monuments Office AMO
1	Resident Architect RDA				1	ForPurcell


PURCELL 🗍

Continuation Page



Above, photo taken on 30th July 2009, dotted line showing the Transfer Gate "A" within A Hall Yard.



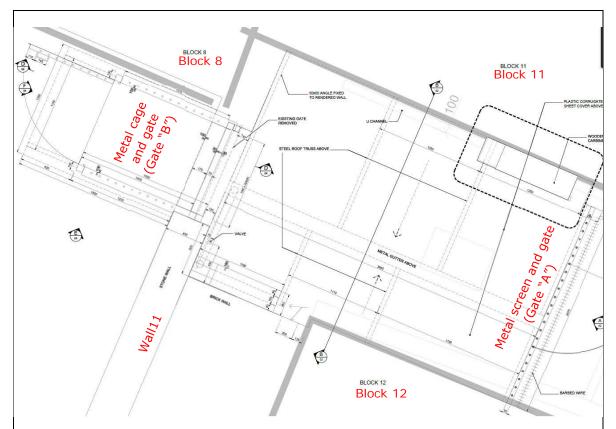

Above, cartographic drawing produced in 2012 showing the location of gates A within A Hall Yard.



This Site Memorandum confirms a variation of the Works following oral instructions, an inspection of site operations or the issuance of new or revised documents for construction. Unless stated otherwise, it shall be treated as an Instruction to carry out works as authorised by Architects Instruction F-620 dated 12 March 2014. Where applicable, it includes provision for distribution to all relevant members of the client/design/construction team and the Antiquities and Monuments Office.

Site Memorandum No. 1067

Date: 1st May 2017

To: Gammon Construction Limited For the attention of: Cliff Leung

Subject: Non-Compliance, Damage to Hopper from Block 9 West Elevation

A.I. no: F-620

NON-COMPLIANCE WITH CONTRACT DOCUMENTS, DAMAGE TO HISTORIC FABRIC

The rainwater hopper from Block 9 west elevation was instructed to be salvaged, redecorated and reinstalled. However, we were notified on 27th April 2017 that the hopper was damaged due to improper storage.

The Management Contractor and Works Package Contractor 601, Hsin Chong Aster are required to:

- Submit proposals to repair the damaged hopper within 14 days of this notice. If repair is not possible, notify the Conservation Architect and fabricate new cast iron rainwater hopper to match existing profile. No work is to be carried out without approval from the Conservation Architect.
- 2. Review and revise the work practices of the works package contractors especially storage of historic fabric.
- 3. Supervise the work operations to ensure compliance with the Contract Documents.

(Continued overleaf.)

Heritage Impact: Historic fabric is damaged.

Proposed Mitigation Measures: Instruct the Contractor to comply with contract documents. Contractor is to submit proposals to repair the damaged hopper. If repair is not possible, fabricate new cast iron rainwater hopper to match existing profile.

Justification: N/A

Variation: N	RLB Cost estimate:	JCCPS	
	HKD	approved/rejected	
Cost implication: N	Initials:	Initials:	
	Date:	Date:	

Copies to:

1	Employer JCCPS	1	Structural Eng A	rup		
1	Quantity Surveyor RLB	1	Services Eng	JRP	٧	Environmental Management ERM
V	Contract Administrator RDA	٧	Design Consultant H	ldM	1	Antiquities & Monuments Office AMO
V	Resident Architect RDA				V	For Purcell



Continuation Page

For information:



Above, photo taken on 17th August 2011, showing the historic hopper at its location.



Above, photo taken on 22nd January 2015, showing the hopper being salaved from the building.

PURCELL 🗍



Above, photo taken on 27th April 2017, showing the hopper was damaged.

Annex M2

A Summary of Condition of Character Defining Elements, Historic Buildings and Structures

Schedule of Character Defining Elements

CENTRAL POLICE STATION, HONG KONG

SCHEDULE OF CHARACTER DEFINING ELEMENTS

This Schedule of Character Defining Elements has been prepared at the request of the Antiquities and Monuments Office (AMO) to support applications for S.6 approval under the Antiquities and Monuments Ordinance and the Environmental Impact assessment Ordinance. The levels of significance and their meanings are derived from the work of James Semple Kerr.

For each element, the level of significance is stated, together with the planned outcome and associated mitigation measure, where applicable, and the resultant impact upon the significance. Generally, only those items subject to change are noted, and the impacts should be read as negative. Where elements are deemed currently to be adverse, the impact of the changes should be read as positive.

The levels of significance and definitions as defined by Kerr are stated below. The criteria used to assess the significance of each element are, as directed by AMO: (i) the association with the operation of the Central Police Station Compound; and (ii) its architectural quality. Where these criteria conflict, the resultant assessment score is aggregated.

Each entry in the schedule is accompanied by a photograph of a sample of the item described. The location of each photograph is noted on the floor plans attached in the appendix to the schedule. Similar examples of each item can be seen by observation.

Schedule of Character Defining Elements

	Level of significance	Meaning			
	Exceptional	Where an individual space or element is assessed as displaying a strong contribution to the overall significance of the place. Spaces, elements or fabric exhibit a high degree of intactness and quality, though minor alterations or degradation may be evident.			
Positive	High	Where an individual space or element is assessed as making a substantial contribution to the overall significance of the place. Spaces, elements or fabric originally of substantial quality, yet may have undergone considerable alteration or adaption resulting in presentation which is either incomplete o ambiguous. The category also includes spaces, elements or fabric of average quality in terms of design and materials, but which exhibit a high degree of intactness.			
	Moderate	Where an individual space or element is assessed as making a moderate contribution to the overall significance of the place. Spaces, elements or fabric originally of some intrinsic quality, and may have undergone alteration or degradation. In addition, elements of relatively new construction, where the assessment of significance is difficult, may be included. This category also includes original spaces, elements or fabric of any quality which have undergone extensive alteration or adaption.			
	Low	Where an individual space or element is assessed as making a minor contribution to the overall significance of the place, especially when compared to other features. Spaces, elements or fabric originally of little intrinsic quality, any may have undergone alteration or degradation. This category also includes original spaces, elements or fabric of any quality which have undergone extensive alteration or adaption to the extent that only isolated remnants survive (resulting in a low degree of intactness and quality of presentation).			
	Neutral	Where an individual space or element is assessed as having an unimportant relationship with the overall significance of the place. Spaces, elements or fabric are assessed as having little or no significance.			
	Adverse	Where an individual space or element detracts from the appreciation of cultural significance, by adversely affecting or obscuring other significant areas, elements or items.			

Central Police Station

Schedule of Character Defining Elements

Central Police Station

Addendum	Date
Item no. 10.029 edited entry	18 June 2013
Item no. 10.030 added	18 June 2013

01 Police Headquarters

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.001	Flat plywood ceiling lining with plain rectangular cover battens		Adverse	Replace with T&G boarding to match existing	Not applicable	High
01.002	Plaster coving at abutments of walls and ceilings		Low	Remove in exceptional cases eg, where adjacent new lift shaft	Cut back neatly to a square edge and ensure remaining section is secure.	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.003	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
01.004	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.005	Plaster box cornice		Moderate	Remove in exceptional cases eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate
01.006	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re- used.	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.007	External shutters		High	Reinstate to match existing pattern	Not applicable	High
01.008	External terraces at 1/F		High	Overlay existing concrete paving with timber deck to provide level access	New deck to be reversible	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.009	Plaster ceilings on GF and LG1		Moderate	Install cloud ceilings to accommodate new services	Install fixed grid to minimise damage to ceiling	High
01.010	Timber door frames and architraves		Moderate	Conceal in exceptional cases eg. where adjacent new lift shaft	Retain architrave and door frame in situ. Avoid damage to joinery.	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.011	Concrete floor		Low	Replace where new kitchens and plant rooms to be installed	Carefully remove and retain existing floorboards for re-use. Ensure controlled demolition of concrete structure and removal of debris from building to avoid damage to adjacent surfaces. Protect or carefully remove and set aside adjacent elements such as skirting boards	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.012	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.013	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.014	Existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non-combustible sheet linings to block opening.	Moderate
01.015	Existing walls		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.016	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
01.017	Mezzanine floor in room 01/LG1/13		Adverse	Remove floor and supporting columns to re-create original double-height space	Not applicable	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.018	Cast iron grilles above Service Corridor 01/LG1/35		High	Remove existing steel sheet covering [alterations to grilles awaiting confirmation from HdM]		
01.019	Perforated concrete deck above lightwell		Adverse	Remove deck and make good brickwork at abutments	Not applicable	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.020	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
01.021	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non-compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.022	Main corridors		High	Install new lighting, fire sprinklers, fire doors to comply with Fire Services Code	New fittings to be mounted in a manner that is of its time and reversible. Avoid physical intervention with existing plaster box cornices, architraves, dado rails	High
01.023	Painted signs	LOCKET	High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.024	Fixed signs	The Control of the Co	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.025	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material in a neutral mid-tone.	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.026	Enclosure at First Floor landing of main stair		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.027	Steel railing enclosure at FF level		Low	Remove	Record on measured drawings and photographs	Low
01.028	Tongued and grooved flat and sloped timber boarded ceilings		Moderate	Repair where necessary and reinstate where missing	Not applicable	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.029	Modern partitions		Adverse	Remove	Not applicable	High
01.030	Tiled dado		High	Cut away for enlargement of existing windows to form new doorways	Cut back to joint line and adjust tiling pattern to suit new opening. New tiles to match existing sizes and colours.	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.031	Reinforced concrete canopy and sash windows		Moderate	Remove canopy and replace sash windows with new windows to match original	Make good brickwork where canopy removed, Reinstate rendered architraves around new window to match similar window facing on West wing	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.032	Arched opening in brick wall above ceiling line		Low	Retain insitu and use to pass through future services. Infill only where opening is within a fire compartment	Use non-combustible material to block opening.	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.033	Ceiling void service installation (Cast Iron Water Tank and pipework)		Low	Remove and make good adjacent surfaces	N/A	Low

02 Armoury

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
02.002	Modern internal doors		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.003	Modern partitions		Adverse	Remove	Not applicable	High
02.004	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

Schedule of Character Defining Elements

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.005	Brickwork walls enclosing rooms at GF and FF East side		Low	Remove and reinstate verandah	Not applicable	High
02.006	Concrete floors		Low	Selected removal to accommodate new stairs and lift shaft	Carefully form openings to ensure structural stability	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.007	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.008	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.009	Concrete stairs		Adverse	Remove stairs	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.010	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts to reduce impact. Finish ducts in a non-reflective material that is neutral in colour and mid-tone.	High
02.011	Roof structure and tiled soffit		High	Repair and retain.	N/A	Neutral

03 Barracks Block

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
3.002	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where item cannot be re-used.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.003	External shutters		High	Reinstate to match existing pattern	Not applicable	High
03.004	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.005	Timber spandrel panels below windows		Low	Conceal in exceptional cases eg. where adjacent new lift shaft	Retain frame and spandrel panel where possible. Remove only where necessary in connection with replanning of interiors. Record on measured survey drawings.	Low
03.006	Timber floors		High	Replace where new kitchens and plant rooms to be installed	Limit extent of removal as much as possible. Carefully remove and retain existing floorboards for re-use. Ensure controlled dismantling of timber structure and set aside for possible re-use. Protect or carefully remove and set aside adjacent elements such as skirting boards	Medium

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.007	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.008	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
03.009	Block existing door openings		Low	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.010	Form new door openings		Low	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance. Re-open original openings where possible. Retain original reveals and arches.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.011	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.012	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
03.013	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.014	Painted signs	NO VISITOR WILL BE ADMITTED WITHOUT THE PERMISSION OF THE D.O. OR FORMATION COMMANDER 或官管主得未如者转探 進擅得不可許官警值當	High	Protect in situ	Not applicable	N/A
03.015	Fixed signs	NO. 3 PLATOON R. & F CHANGING ROOM 第三隊更衣室	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.016	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
03.017	Lean-to structure adjacent North wall		Moderate	Remove	Record on measured survey drawings. Make good walls where roof structure abuts	Moderate

Schedule of Character Defining Elements

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.018	Metal-frames windows at GF North elevation		Adverse	Remove window frames, masonry spandrel panels below and reinstate verandah	Not applicable	High
03.019	Internal walls at Ground Floor level		Moderate	Remove selected internal walls where strictly necessary as part of replanning of interiors	Walls of early or original date to be retained in part eg. by leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded. Record walls on measured survey dwgs.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.020	Assembly rooms at centre of building (all floors)		Moderate	Sub-divide two rooms on each floor to provide service core, comprising: lifts, toilets, plant rooms, stores	Form new sub-visions using lightweight partitions to achieve reversibility. Form straight joints at abutments with existing retained walls. Notch new partitions around existing brick corbels at high level as a reminder of current condition.	Moderate
03.021	Exposed soffits of timber floors		Moderate	Underline existing floors to achieve specified fire resistance stated in Code	Avoid unnecessary damage to existing structure. New lining will reduce extent of intervention into existing structure. Keep level of new linings well clear of window heads.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.022	Existing window frames/openings		High	Open up selected openings to form new fire escape doors	Retain any salvageable material for possible reuse elsewhere. Retain existing window jambs intact. Cut away masonry to form door openings along same line as window jamb; do not re-bind cut brickwork. Record existing condition on measured survey drawings.	Low
03.023	Single storey outbuildings on south side		Adverse	Demolish	Check for evidence of early route from Magistracy to Prison.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.024	Bridge at east end		Moderate	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.025	Chimneypiece on Ground Floor		Low	Repair and retain in current location	Not applicable	Neutral
03.026	Window in south wall; original dormitory space		Moderate	Remove window and take down brickwork spandrel; subdivide space to form new fire-protected escape route.	Record existing condition on measured survey drawings. New partition wall to be reversible.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.027	Clay-tiled floor in store room adjacent stairs		Low	Remove as part of replanning of interiors	Record on measured survey drawings	Low

04 Dormitory Block A & B

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
04.002	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.003	Plaster box cornice		Moderate	Remove in exceptional cases where eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.004	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.005	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.008	Altered doors and windows	BLOCK B	Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.009	Window frames in arcades of North and East elevations		Adverse	Remove window frames and make good masonry reveals and reinstate verandah	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.010	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.011	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.012	Stair from First to Second Floor		High	Replace stair to improve safety	New stair to be built of steel to comply with Code and to distinguish it as being "of its time".	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.013	External verandahs	The state of the s	High	Install new lighting, fire sprinklers, fire doors to comply with Fire Services Code, extract ducting to external walls	New fittings to be mounted in a manner that is of its time and reversible. Avoid physical intervention with existing plaster box cornices in rooms, architraves, dado rails. Position outlet grilles in extneral walls on centreline of arcade arches and above structural arch	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.014	Painted signs	BLOCK A	High	Protect in situ	Not applicable	N/A
04.015	Fixed signs		Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.016	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.017	Toilets at ends of verandahs		Adverse	Remove and make good finishes	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.018	Partitions at GF Dormitory A		High	Remove to make way for Interpretation	Prepare measured drawings and photographs before removal.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.019	Switchgear in old porch 04/G/13		Adverse	Open up porch, remove electrical switchgear and make good	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.020	Flat plywood ceiling lining with plain rectangular cover battens		Adverse	Replace with T&G boarding to match existing	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.021	Steps up to doorway on FF verandah	EXITED	Moderate	Remove steps and doorway to form new fore escape route	Record steps and doorway on measured drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.022	Timber boarded floors with moulded skirtings		High	Retain all boarded floors and skirtings	Reinstate floor boards and skirtings after fire proofing works	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.023	Cantilever balconies		High	Retain and repair as necessary. Reinstate balcony on west elevation.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.024	Clay tile floor		Low	Retain and repair as necessary	Not applicable	Neutral
04.025	Matched- boarded ceiling with perforated border		Moderate	Repair and retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.026	Ceiling rose		Low	Repair and retain insitu	Not applicable	Neutral

06 Dormitory C

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.001	Granite thresholds at external doors		Low	Retain; install timber deck flush with level of step where necessary	Avoid alteration to step.	Low
06.002	Pitched roof		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.003	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High
06.004	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.005	Altered doors and windows		Adverse	Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable
06.006	External airconditioning units and other external services		Adverse	Adverse	Remove and make good brickwork	Not applicable

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.007	Painted signs	PECKC.	High	Protect in situ	Not applicable	N/A
06.008	Fixed signs	衛生署 DEPARTMENT OF HEALTH 中央警署診療所 POLICE MEDICAL POST CENTRAL POLICE STATIN	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.009	Cantilever balconies		High	Retain and repair as necessary.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low
06.010	Iron balustrades		High	Retain and repair as necessary.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.011	Perforated margin at perimeter of ceiling	EXIT ED	Low	Repair and retain.	Where fire-proofing of floor is required, use a product that can be installed within the floor void, leaving the ceiling lining intact.	Low
06.012	Block existing door openings	EXIT	Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non-combustible sheet linings to block opening.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.013	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate
06.014	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.015	Timber floors		High	Retain all boarded floors and skirtings	Reinstate floor boards and skirtings after fire proofing works	Low
06.016	Vinyl tile floor		Adverse	Remove tiles; renew boarded floor boards if necessary	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.017	Batten and panel ceiling lining		Low	Replace with lath and plaster ceiling	Not applicable	Low
06.018	Exposed roof covering		Moderate	Retain as existing	Consider insulating between upper and lower layers of roof tiles to provide thermal insulation and vapour barrier	Low

07 Dormitory D

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.001	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
07.002	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
07.004	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.005	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
07.006	Clothes drying racks		Adverse	Remove	Not applicable	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.008	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
07.009	Corbelled brickwork at perimeter of room		Low	Remove in exceptional cases where eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.010	Plywood floor		Adverse	Replace with hardwood floor boards	Not applicable	High
07.011	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.012	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate
07.013	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.014	Fixed signs	P 学 子 分 体 所 Control Price Station Redicts But	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.015	Exposed roof tiling		Moderate	Retain as existing	Consider insulating between upper and lower layers of roof tiles to provide thermal insulation and vapour barrier	Low
07.016	Concrete floor		Adverse	Overlay with hardwood floor boards	Not applicable	Moderate

08 Ablutions Block

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.001	Panelled doors		Low	Replace where necessary to achieve compliance with Building Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate
08.002	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
08.004	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non- combustible sheet linings to block opening.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.005	Timber roof structure		High	Retain	Not applicable	Neutral
08.006	External stair at west end		Moderate	Retain	Repair as necessary. Alter balustrade to achieve reasonable level of operational safety. Restrict access to repairs and maintenance and means of escape.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.007	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
08.008	Painted signs	NO VISITOR WILL BE ADMITTED WITHOUT THE PERMISSION OF THE D. D. OR FORMANION COMMANDER 支管主導体和者珍様 連接将不可計官擊血當	High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.009	Wire mesh screens		Adverse	Remove	Not applicable	Low
08.010	Internal walls and concrete floors		Low	Remove and rebuild in new configuration to suit new use	Ensure retained facades are fully supported during construction operations. Protect retained walls against damage during demolition works. Install new walls and floors to respect fenestration; avoid	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
					clashes.	
08.011	Cantilever balconies on north side		Moderate	Repair and retain insitu	Not applicable	

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.012	Bridge access to Barrack Block		Moderate	Retain	Repair as necessary. Alter balustrade to achieve reasonable level of operational safety. Restrict access to repairs and maintenance and means of escape.	Low
08.013	Balcony balustrades		Low	Repair as necessary and retain. Remove selected sections to enable installation of new bridge connections to Barrack Block.	Avoid removal of associated iron columns. Form interventions at selected positions so as to maintain the rhythm of the balustrades and ensure proper support at ends.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.014	Single-storey outbuilding with pitched roof over		Low	Demolish to make way for new loading bay.	Record on measured survey drawings. Infill existing internal opening leaving reveals exposed. Tooth-in new brickwork at abutments after existing walls removed. Salvage cast iron columns for possible re-use.	Low
08.015	Corrugated steel sheet on balcony balustrades		Adverse	Remove	Not applicable	Low

Schedule of Character Defining Elements

Central Police Station

09 Magistracy

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
09.002	Modern partitions		Adverse	Remove	Not applicable	N/A

Schedule of Character Defining Elements

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.003	Internal walls		Moderate	Remove selected internal walls where strictly necessary as part of replanning of interiors	Walls or early or original date to be retained in part eg. By leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded, as evidence of the current condition.	Moderate
09.004	Plaster box cornice		Moderate	Remove in exceptional cases eg. Where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.005	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Moderate
09.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.008	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate
09.009	Fixed signs	WINDOWS DEPARTMENT RESOLUTION DEPARTMENT RE	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.010	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
09.011	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.012	Rainwater goods		Moderate	Replace with larger sizes/closer spacing to improve performance	Use cast iron to match original pattern Make good all redundant fixing holes	High
09.013	Metal walkways across lightwell		Adverse	Remove walkways and make good brickwork at abutments	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.014	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
09.015	Sloping canopy over external stair on west side		Adverse	Remove canopy and supporting structure	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.016	Single storey secure shelter at North West corner		Low	Demolish	Make good brickwork at abutments.	Low
09.017	Iron railing adjacent south side of item 09.016 above		Moderate	Retain; including remains of bars (now removed) between existing railings and east side of Barracks Block.	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.018	Public toilets in 09/LG1/17, 24		Adverse	Strip out sanitaryware, and fit-out for pottery display/service access. Form new door openings in east walls.	Retain existing door openings and metal- barred gates. Retain external granite steps and existing ground level.	Low
09.019	Cell doors		High	Re-open to provide access to Retail space	Retain existing iron gate	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.020	Meeting room at G/02-05		Moderate	Remove timber panelling from walls and sub divide to form new toilets and lift shaft	Record existing wall linings, and any earlier lining behind, on measured survey drawings.	Moderate
09.021	Lobbies within entrance hall G/12		Adverse	Remove	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.022	Public galleries on FF		Adverse	Strip out plant, remove partition walls and restore galleries	Not applicable	High
09.023	Chimney piece		Moderate	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.024	Lanterns above entrance hall		Adverse	Remove existing lanterns and install single lantern	Not applicable	Moderate
09.025	Boarded ceilings on Second Floor		High	Repair and retain where possible	Limit extent of penetrations as far as practicable. Record on measured survey drawings where ceilings have exceptionally to be removed.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.026	Iron gates at top of external stair		Moderate	Retain	No applicable	Neutral
09.027	Iron balustrade adjacent terrace at First Floor east side		High	Retain; install structural glass balustrade inboard of ironwork to provide compliance with Building Codes	Avoid penetration of existing tiled pavement when fixing glass balustrade.	Low

10 Assistant Superintendent's Office

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
10.002	Plaster box cornice		Moderate	Remove in exceptional cases eg. Where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.003	Panelled doors and linings	No. 1272.	Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.004	Timber boarded floor with moulded skirtings		High	Repair as necessary and retain	Lift carefully and refix upon completion of fire- proofing and services installation	Low
10.005	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening.	Moderate
10.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.008	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
10.009	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.010	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.011	Fixed signs	は、大きない。 は、たるない。 は、なない。 は、なななななななななななななななななななななななななななななななななななな	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
10.012	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.013	Internal walls		Moderate	Remove selected internal walls where strictly necessary as part of replanning of interiors	Walls or early or original date to be retained in part eg. By leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded, as evidence of the current condition.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.014	Partitions on SF		Moderate	Remove partitions	Record partitions on measured drawings	Moderate
10.015	Blocked windows on south elevation of south-east wing		Adverse	Re-open window openings and reinstate window frames and glazing	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.016	Open-joisted ceiling on Ground Floor of south- east wing		Moderate	Underline floor to provide fire protection.	Avoid intrusive alteration. Use fire-proofing products and methods that enable existing structure and boarding to be retained.	Low
10.017	Moulded timber picture rail		Low	Repair and retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.018	Timber roof structure above south-east wing		Moderate	Repair as necessary and retain	Avoid intrusive alteration. Retain open appearance/	Low
10.019	Timber stair		Moderate	Underline with fire- resisting lining	Repair as necessary and retain.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.020	Clay/terrazzo tile floor on Ground Floor and steps		Adverse	Adjust levels to enable level access and replace floor finish	Not applicable	Low
10.024	Granite wall on North elevation		High	Construct new external steps adjacent wall	Keep new stair clear of wall; avoid any physical connection between steps and wall.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.025	Single storey outbuilding at South East corner		Moderate	Demolish outbuilding and make good at abutments	Record outbuilding on measured drawings	Low
10.026	Blocked archway on East elevation		Adverse	Demolish infilling and reopen archway	Protect original arch and jambs against damage during demolition	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.027	Chimney on east elevation		Low	Retain	Not applicable	Neutral
10.028	Cantilever balconies		High	Repair as necessary and retain	Avoid intrusive interventions. Restrict access if necessary to retain existing appearance.	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.029	Steps on east elevation		Moderate	Repair as necessary and retain	Not applicable	Neutral
10.030	Decorative metal screen (See also item 10.026)		Low	Repair and retain	Not applicable	Positive

11 A Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.001	Form new door openings		Low	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.002	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
11.003	Painted signs	AHALL	High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.004	Fixed signs	多生 小心地滑 CAUTION SLIPPERY FLOOR	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
11.005	Concrete stairs		Low	Remove and rebuild as part of re-planning of interiors	None	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.006	Flat roof		Low	Form new rooftop extension at West end to accommodate fire escape stair	Form straight joint at abutment with building 08 Ablutions Block	Low
11.007	Security screen at roof level		Low	Remove	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.008	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.009	Rainwater goods		Low	Remove embedded cast iron pipework set into wall to reduce long term maintenance burden	Record on measured survey drawings. Make good cavity.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.010	Timber doors		Low	Repair and retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.011	Security screen and door at First Floor	EXITHO	Low	Remove	Record on measured survey drawings	Low
11.012	Door thresholds and plinth		Low	Retain; remove paint media from plinth and brickwork	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.013	Metal louvres on window openings		Adverse	Remove	Not applicable	Low

12 B Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.001	Flat roof		Moderate	Repair and retain	Avoid roof penetrations as far as possible	Low
12.002	Cells at GF level		High	Remove cells in selected locations to accommodate new North-South route across site	Record existing layout on measured survey drawings. Limit number of cells affected to the minimum necessary. Retain floor structure above. Retain remainder of cells at this level for interpretation	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.003	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
12.004	Painted signs	BUAL	High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.005	Fixed signs	The state of the s	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
12.006	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

Schedule of Character Defining Elements

Central Police Station

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.007	Corbelled brickwork at high level in cells		Low	Retain	Not applicable	Neutral
12.008	Barbed wire		Moderate	Remove	Record wire on measured drawings	Low

Schedule of Character Defining Elements

Central Police Station

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.009	External walls		Moderate	Form openings in North and South walls in conjunction with new North-South route across site	Cut brickwork to form openings in North and South walls; do not re-bond brickwork.	Moderate

13 C Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.001	External airconditioning units and other external services		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.002	Door to Ladder Store		Low	Retain	Not applicable	Neutral
13.003	Security bars at window openings		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.004	Flat roof		Low	Retain	Avoid roof penetrations as far as possible.	Low
13.005	Eaves detail		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.006	Cantilever reinforced concrete canopy		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.007	Internal partition walls		Low	Remove as part of replanning of interiors	Record on measured survey drawings	Low
13.008	Fixed signs	Note that the second of the se	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.009	Metal window frames		Moderate	Repair and retain	Not applicable	Neutral
13.010	Internal security screens		Moderate	Retain where possible	Where necessary record on measured survey drawings prior to removal	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.011	Coving at abutments between RC beams and walls		Low	Avoid penetrations for services installations as far as possible.	Cut away neatly for services penetrations and make good at abutments.	Low
13.012	Communal cells at Ground Floor		Moderate	Remove as part of re- planning of interiors	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.013	Rooflight and security bars over communal cells		Moderate	Remove as part of replanning of interiors	Record on measured survey drawings	Low
13.014	Granite threshold at external door openings		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.015	Timber boarded doors with fanlight over		Low	Repair as necessary and retain	Not applicable	Neutral
13.015	Vinyl tile floor		Adverse	Replace	Not applicable	Low

Schedule of Character Defining Elements

Central Police Station

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact

14 D Hall East Wing

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.001	West entrance at Lower Ground Floor		Moderate	Retain as public entrance at this level.	Retain security gate and granite threshold. Adjust adjacent ground level as necessary to achieve barrier-free access. Pin gate back against adjacent wall in the open position if necessary.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.002	Half-round headed doorway and side lights		Moderate	Retain	Remove air duct and make good masonry above arch.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.003	Granite surround to cells (generally north side, alternating with brick surrounds – see next item)	3	Moderate	Retain door surround and gate wherever possible.	Pin back gate against wall. Remove paint media to expose granite material.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.004	Brick reveals with bull-nosed arrisses and segmental arch over (generally north side, alternating with granite surrounds – see previous item)		High	Retain door surround and gate wherever possible	Pin back gate against wall	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.005	Arched opening at East end First Floor		Low	Retain as existing	Not applicable	Low
14.006	Concrete floor generally at Lower Ground Floor		Low	Excavate entire floor to install piled underpinning	Record levels on measured survey drawings. Install new floor at the same level.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.007	Part-blocked windows at Lower Ground Floor - extent of blocking varies.		Moderate	Open up window opening to full extent.	Record existing condition on measured survey drawings. Add further detail during demolition works.	Low
14.008	External granite stair from Lower Ground to Ground Floor level		Moderate	Remove stair to make way for new stair in similar position	Review design proposals to see whether existing stair can be retained.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.009	Ashlar pattern on external walls		Moderate	Form new openings for entrance/exit to building	Set out new openings to cause minimum disruption to ashlar pattern. Record existing pattern on measured survey drawings.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.010	Blocked doorway at south-east corner		Low	Preserve blocked opening intact.	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.011	Metal security gate and screen		Low	Retain insitu	Pin gate in open position if necessary	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.012	Half-round headed doorway and side lights at Ground Floor west end		Moderate	Retain insitu	Not applicable	Neutral
14.013	Structural steelwork bracing and temporary access stair		Adverse	Remove upon completion of underpinning	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.014	RC staircase at north-east corner		Low	Remove	Record on measured drawings	Low
14.015	Vinyl tile floor on suspended timber floor		Adverse	Remove vinyl tiles and restore boards if possible; alternatively, replace boards with new timber to match other boarded floors elsewhere on the site.	Not applicable	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.016	Cell walls at Ground Floor		Moderate	Retain insitu	Use existing door openings wherever possible. Avoid further alteration to existing altered openings where feasible.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.017	Mortuary		High	Preserve insitu	Avoid any service penetrations from adjacent spaces	Neutral
14.018	Brickwork surrounds to doorways with segmental arches over		Moderate	Increase width in selected locations to allow wheelchairs to pass	Record on measured survey drawings. Limit interventions as far as possible.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.019	Granite surrounds to doorways with lintels over		Moderate	Increase width in selected locations to allow wheelchairs to pass	Record on measured survey drawings. Limit interventions as far as possible.	Low
14.020	Flat ceilings at Ground Floor	A	Low	Form penetrations for services installations where necessary	Avoid disruption of beams.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.021	Arched opening at east end		Low	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.022	Top-lit central hall		High	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.023	Arches across central hall at First Floor		Moderate	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.024	Inset security gate and screen in First Floor cells		Low	Remove to suit new use	Remove where necessary. Record on measured drawings.	Low

14 D Hall West Wing

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.030	Main stair		High	Remove wire mesh and framing	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.031	Brick vault over central hall at Ground Floor		High	Retain insitu	Not applicable	Neutral
14.032	Terrazzo floor in central hall at Ground floor		Moderate	Remove to enable piled underpinning	Record on measured survey drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.033	Brick vaults above cells		High	Retain insitu	Avoid penetrations for services	Neutral
14.034	Cell walls (later additions)		Moderate	Remove where necessary to accommodate new cafe	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.035	Brickwork spandrels below cell windows on south side at Ground Floor		Moderate	Remove to accommodate new cafe	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.036	Cell walls flanking central hall		High	Remove to accommodate new cafe	Record on measured survey drawings. Retain selected cells for interpretation purposes.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.037	Cell floors		Low	Remove to enable piled underpinning	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.038	Partition wall across central hall at Ground Floor		Low	Remove to accommodate new cafe	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.039	Granite pavement in cross-passage between East and West Wings		Moderate	Repair as necessary and retain insitu	Not applicable	Neutral
14.040	Granite threshold at doorway between cross- passage and East Wing		Moderate	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.041	Brick vault over cross-passage		High	Retain insitu	Avoid any services penetrations	Neutral
14.042	Granite floor in central hall at First Floor		Moderate	Retain insitu	Repair where necessary	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.043	Cell walls flanking central hall at First Floor		High	Retain insitu	Not applicable	Neutral
14.044	Brickwork spandrels below cell windows at Second Floor		Moderate	Remove to enable new use	Record on measured drawings. Confine changes to one elevation, north or south.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.045	Metal security screen adjacent main stair		Moderate	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.046	Double-height central hall at Second Floor		High	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.047	View ports adjacent entrance doors		Moderate	Retain insitu	Not applicable	Neutral
14.048	Services installations		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.049	Metalwork and structural steel framing on exterior (typical)		Adverse	Remove	Not applicable	High
14.050	Blind arcade, south elevation		Low	Remove infill brickwork within arched openings at ground level to enable new cafe	Record on measured survey drawings. Observe and record any evidence that brickwork infills were built at the same time as the arched openings or added later	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.051	Blind arcade, north elevation		Low	Retain insitu	Not applicable	Neutral
14.052	Fence wall, east end of D Hall Yard		Low	Remove to reinstate access to granite stair to Lower Ground Floor level	Record on measured drawings	Low

15 E Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.001	Dividing walls at Lower Ground Floor	HAIR AND THE PARTY OF THE PARTY	Moderate	Remove to enable multi- purpose use	Record on measured survey drawings	Low
15.002	Dividing walls at Lower Ground Floor		Moderate	Remove to enable multi- purpose use	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.003	Staircase within Laundry Yard		Moderate	Remove to enable construction of Arbuthnot Wing	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.004	Services installations	Tart	Adverse	Remove	Not applicable	Moderate
15.005	Metal louvres over cell window openings		Low	Remove	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.006	Raised ground level adjacent entrance		Low	Remove to enable level access	Record on measured survey drawings	Low
15.007	Access balconies and apertures		Moderate	Retain apertures	Provide temporary closure as required for operational reasons	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.008	Central staircase		High	Retain	Provide secondary staircase within cell blocks to achieve code compliance	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.009	Cell walls flanking central hall		High	Retain	Pin back cell doors against walls.	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.010	Services installations	Add BODDO	Adverse	Remove	Not applicable	Moderate
15.011	Balcony balustrades		Moderate	Retain	Install wire net across aperture to avoid need to upgrade balustrade to meet Building Code requirements	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.012	Second Floor central hall		High	Retain	Not applicable	Neutral

17 F Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.002	Rainwater goods		Low	Remove existing RWPs and install new RWPs externally on North and South Elevations	Improve roof drainage to avoid ponding	Low
17.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.004	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
17.005	Fixed signs	PRISONERS' PRIVATE CLOTHING STORE 犯人私家衣服儲藏室	Moderate	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.006	Security screen at First Floor entrance		Low	Remove	Record on measured drawings	Low
17.007	Metal windows		Moderate	Remove at First Floor to accommodate gallery space and block structural openings with blockwork	Record on measured drawings.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.008	Fixed furniture		Moderate	Remove to accommodate gallery space	None	Low
17.009	Security screens		Moderate	Remove to accommodate gallery space	Record on measured drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.010	Timber windows		Moderate	Remove at First Floor to accommodate gallery space and block structural openings with blockwork	Record on measured drawings	Moderate
17.011	Communal washing/lavatory facilities		Moderate	Remove to accommodate gallery space	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.012	Blocked up lantern light		Low	Unblock lantern and fit glazing	Record on measured drawings	Low
17.013	Security gates at Ground openings		Moderate	Remove to enable access to Ground Floor gallery space	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.014	Interview booths		High	Remove to accommodate new gallery	Rebuild in new location	Moderate
17.015	External stair to First Floor		Moderate	Upgrade balustrade to comply with Building Code	Record on measured drawings. Supplement existing balustrade elements with minimal elements if necessary.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.016	Ground Floor main entrance		Low	Retain as existing.	Keep fixed shut if not required for operational use.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.017	Security screen at Ground Floor main entrance	STATE AND TO STATE OF	Low	Remove to accommodate gallery space	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.018	Blue Entrance Gate (facing Old Bailey Street)		High	Retain in situ	Maintain in working order	Neutral
17.019	Blue Entrance Gate (inner) and enclosed yard		Moderate	Retain gate and enclosing walls and roof in situ; remove cupboards.	Repair and maintain gate in working order	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.020	Blue Entrance Gate (inner) facing Prison Yard		Moderate	Retain gate and enclosing frame	Repair and maintain in working order	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.021	Barbed wire		Moderate	Remove	Record on measured drawings. Make good fixing points where attached to brickwork.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.022	Metal security bars at windows		Moderate	Remove as part of blocking up window openings to accommodate gallery space at First Floor	Record on measured drawings	Low
17.023	External toilets at Ground Floor adjacent East elevation		Low	Remove	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.024	Open Visit Room		Low	Space reallocated to other uses	Record on measured drawings. Salvage entrance sign and re-use in new layout of interview booths.	Low

19 Bauhinia House

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.001	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
19.002	Chimney		High	Repair and retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.003	Rainwater goods and other external services		Adverse	Remove and make good wall surface. Replace defective and non-matching rainwater goods with cast iron fittings to match original.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.004	External stone wall facing		High	Carry out close inspection of painted areas to determine extent of original granite facing and remove paint media where applicable.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.005	Gun loops		High	Remove concrete infilling and make good stonework where necessary.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.006	Look-out turret		High	Repair and retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.007	Windows		Moderate	Remove and make good stonework as necessary	Record existing windows on measured survey drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.008	Modern partitions		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.009	Electrical services	A SERVICE OF THE PROPERTY OF T	Adverse	Remove	Not applicable	Moderate
19.010	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.011	Exposed timber roof structure		High	Repair and retain insitu	Not applicable	Neutral
19.012	Timber stair		Moderate	Remove	Record on measured surveys drawings	Low
