



AUES PROJECT NO. TCS/00704/14

**CONTRACT NO. MTRC6593-13C –
WAN CHAI STATION LEE TUNG STREET SUBWAY**

**27TH ENVIRONMENTAL MONITORING AND AUDIT
(EM&A) MONTHLY REPORT – NOVEMBER 2016**

**PREPARED FOR
KADEN CONSTRUCTION LIMITED**

Quality Index

Date	Reference No.	Prepared By	Approved By
9 December 2016	TCS00704/14/600/R0122v2	 Martin Li Assistant Environmental Consultant	 T.W. Tam Environmental Team Leader

Version	Date	Description
1	7 December 2016	First Submission
2	9 December 2016	Amended against IEC's comments

Your Ref:
Our Ref: 40032976/457031

By Email and Post

MTR Corporation Limited
Fo Tan Railway House
No. 9, Lok King Street, Fo Tan
Shatin, N.T.,
Hong Kong

Attn.: Mr. Kenneth Chow / Environmental Engineer II

12 December 2016

Dear Sirs


**Consultancy Agreement A130-13
Independent Environmental Checker for CRS and LTS
LTS - Verification for 27th Monthly Environmental Monitoring and Audit (EM&A) Report
(November 2016) (Report No.: TCS00704/14/600/R0122v2)**

We refer to the 27th Monthly EM&A Report (November 2016) received under cover of the email from the Environmental Team, AUES, dated on 7 December 2016.

Further to our comments provided on 9 December 2016 and subsequent revision of the Report by AUES on 9 December 2016, we have no further comment and have verified the captioned report (Report No.: TCS00704/14/600/R0122v2).

Should you have any queries, please feel free to contact the undersigned at 3922 9366.

Yours faithfully
AECOM Consulting Services Ltd



Y. W. Fung
Independent Environmental Checker

LLMC/wwsc

cc Kaden Consturction Limited (Attn.: Mr. Ronald Fung) via email
AUES (Attn.: Ms. Nicola Hon) via email

EXECUTIVE SUMMARY

ES01 This is the 27th monthly EM&A Report presenting the monitoring results and inspection findings for the period from **1 to 30 November 2016** (hereinafter ‘the Reporting Period’).

SUMMARY OF ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES02 The monitoring and audit activities during the Reporting Period are summarized in below:-

Environmental Aspect	Environmental Monitoring Parameters / Inspection	Reporting Period	
		Number of Monitoring Location	Total Occasions
Air Quality	24-hour TSP	1	5
Construction Noise	L _{eq(30min)} Daytime	2	10
Site Inspection Audit	Weekly inspection with ET, the Contractor and RE	--	5
	Monthly joint inspection with ET, the Contractor, RE and IEC	--	1

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES03 In the Reporting Period, no air quality and noise monitoring exceedances were registered. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	24-hour TSP	0	0	0	0	0
Construction Noise	L _{eq(30min)} Daytime	0	0	0	0	0

ENVIRONMENTAL COMPLAINT

ES04 No public complaint was received in the Reporting Period.

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES05 No environmental summons or successful prosecutions were recorded in the Reporting Period.

REPORTING CHANGE

ES06 No reporting changes were made in the Reporting Period.

SITE INSPECTION

ES07 In the Reporting Period, weekly site inspection by the MTRC, ET and Contractor was carried out on **3, 11, 17, 24 and 29 November 2016** and the IEC was joined the site inspection on **29 November 2016**. No non-compliance but four (4) observations and one (1) reminder were recorded during the site inspection.

ES08 It is reported that the transplanted tree TR-02 for this project was collapsed due to typhoon signal No. 8 HAIMA on 22 October 2016 and the tree has been subsequently removed. Further follow-up action will be made after an agreement is reached with Leisure and Cultural Services Department (LCSD).

FUTURE KEY ISSUES

ES09 Construction noise is the key environmental issue during construction work of the Project as there are residential buildings nearby. Noise mitigation measures should be fully implemented in accordance with the EM&A requirement.

- ES010 Special attention should be paid on the potential construction dust impact as the construction site is located near the residential area. The Contractor should fully implement the construction dust mitigation measures properly.
- ES011 The Contractor should prevent muddy water and other water pollutants via site surface water runoff get into public areas and implement water quality mitigation measures properly. Any discharge water should be strictly complied with wastewater discharge license requirement.
- ES012 The Contractor should pay attention and implement sufficient protection to the transplanted tree for this project to avoid any damage done to the transplanted tree and prevent tree collapse in the future.

TABLE OF CONTENTS

1	INTRODUCTION	1
	PROJECT BACKGROUND	1
	REPORT STRUCTURE	1
2	PROJECT ORGANIZATION AND SUBMISSION	2
	PROJECT ORGANIZATION	2
	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	3
3	ENVIRONMENTAL IMPACT MONITORING REQUIREMENT	5
	MONITORING PARAMETERS	5
	MONITORING LOCATIONS	5
	MONITORING FREQUENCY AND PERIOD	5
	MONITORING EQUIPMENT	6
	MONITORING METHODOLOGY	7
	DERIVATION OF ACTION/LIMIT (A/L) LEVELS	8
	DATA MANAGEMENT AND DATA QA/QC CONTROL	8
4	MONITORING RESULTS	9
	24-HOUR TSP AIR QUALITY MONITORING RESULTS	9
	NOISE MONITORING RESULTS	9
5	WASTE MANAGEMENT	10
	GENERAL WASTE MANAGEMENT	10
	RECORDS OF WASTE QUANTITIES	10
6	SITE INSPECTION	11
	FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH	11
7	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	12
	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	12
8	IMPLEMENTATION STATUS OF MITIGATION MEASURES	13
	GENERAL REQUIREMENTS	13
	KEY ISSUES FOR THE COMING MONTH	14
9	CONCLUSIONS AND RECOMMENDATIONS	15
	CONCLUSION	15
	RECOMMENDATIONS	15

LIST OF TABLES

TABLE 2-1	SUBMISSION/SET-UP STATUS OF THE EP REQUIREMENTS
TABLE 2-2	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACTS
TABLE 3-1	SUMMARY OF THE MONITORING PARAMETERS OF EM&A REQUIREMENTS
TABLE 3-2	AIR AND NOISE MONITORING LOCATIONS
TABLE 3-3	AIR QUALITY MONITORING EQUIPMENT
TABLE 3-4	CONSTRUCTION NOISE MONITORING EQUIPMENT
TABLE 3-5	ACTION AND LIMIT LEVELS FOR AIR QUALITY MONITORING
TABLE 3-6	ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 4-1	SUMMARY OF 24-HOUR TSP MONITORING RESULTS – A1
TABLE 4-2	NOISE MONITORING RESULTS OF N1 (2/F FLOOR OF HENNESSEY BUILDING), (dB(A))
TABLE 4-3	NOISE MONITORING RESULTS OF N2 (BALCONY AT 1/F OF CHIU HIN MANSION), (dB(A))
TABLE 4-4	ADJUSTMENT OF CONSTRUCTION NOISE LEVEL FOR N1, dB(A)
TABLE 5-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 5-2	SUMMARY OF QUANTITIES OF NON-INERT C&D WASTES

TABLE 6-1	SITE OBSERVATIONS
TABLE 7-1	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 7-2	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 7-3	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 8-1	ENVIRONMENTAL MITIGATION MEASURES

LIST OF APPENDICES

APPENDIX A	PROJECT SITE LAYOUT PLAN
APPENDIX B	ORGANIZATION OF THE PROJECT AND MASTER CONSTRUCTION PROGRAMME
APPENDIX C	MONITORING LOCATIONS
APPENDIX D	CALIBRATION CERTIFICATE OF MONITORING EQUIPMENT
APPENDIX E	HOKLAS-ACCREDITATION CERTIFICATE OF THE TESTING LABORATORY
APPENDIX F	EVENT AND ACTION PLAN
APPENDIX G	MONITORING SCHEDULE
APPENDIX H	DATABASE OF MONITORING RESULTS
APPENDIX I	GRAPHICAL PLOTS
APPENDIX J	METEOROLOGICAL INFORMATION
APPENDIX K	MONTHLY SUMMARY WASTE FLOW TABLE
APPENDIX L	IMPLEMENTATION SCHEDULE FOR ENVIRONMENTAL MITIGATION MEASURES (ISEMM)

1 INTRODUCTION

PROJECT BACKGROUND

- 1.01 **KADEN CONSTRUCTION LIMITED** (hereinafter ‘KCL’) has been awarded by the MTR Corporation Limited (MTRCL) the Contract No. *MTRC6593-13C – Wan Chai Station Lee Tung Street Subway* (hereinafter “the Project”), which is a Designated Project to be implemented under Environmental Permit EP-444/2012 (hereinafter referred as “the EP-444/2012” or “the EP”).
- 1.02 The Project includes redevelopment of the Lee Tung Street area to improve pedestrian networking by enhancing the accessibility, connectivity and circulation of human traffic north-south from Queen’s Road East area to Wan Chai MTR Station, and providing a safe and attractive means for pedestrian crossing of Johnston Road. The Project site layout plan is shown in *Appendix A* and works under the Project comprise of:
- (i) Construction of a pedestrian subway link between Urban Renewal Authority’s Redevelopment at Site H15 (the Development) and Wan Chai Station (WAC);
 - (ii) Construction of two ventilation shafts; and
 - (iii) Modification works of some of the station concourse.
- 1.03 The Project is expected to be undertaken for 36 months. In order to effectively implement the environmental protection measures as stipulated in the Particular Specification (PS), an Environmental Monitoring and Audit Plan (EMAP) which enclosed in the Project Profile (PP) was prepared to guide the setup of the environmental monitoring and audit (EM&A) programme of the Project.
- 1.04 Action-United Environmental Services and Consulting (AUES) has been commissioned by the KCL as the independent environmental team (ET) to implement the relevant EM&A programme for the Project.
- 1.05 The baseline monitoring program was carried out between 3 June 2014 and 19 June 2014 at the proposed monitoring locations by the ET according to the approved EMAP. The “Baseline Monitoring Report (R0010 Version 4)” has been verified by IEC submitted to the EPD on *15 July 2014* before commencement of major construction works. The construction of the Project was commenced on 28 August 2014 as notified by KCL. Accordingly, relevant EM&A programme was started on 28 August 2014.
- 1.06 This is **27th** monthly EM&A report presenting the monitoring results and inspection findings in the Reporting Period from **1 to 30 November 2016**.

REPORT STRUCTURE

- 1.07 This Report is structured into the following sections:-
- Section 1 Introduction*
 - Section 2 Project Organization*
 - Section 3 Environmental Impact Monitoring Requirement*
 - Section 4 Monitoring Results*
 - Section 5 Waste Management*
 - Section 6 Site Inspections*
 - Section 7 Environmental Complaint and Non-Compliance*
 - Section 8 Implementation Status of Mitigation Measures*
 - Section 9 Conclusions and Recommendations*

2 PROJECT ORGANIZATION AND SUBMISSION

PROJECT ORGANIZATION

2.01 The project organization is shown in *Appendix B*. The responsibilities of respective parties are:

MTR Corporation Limited (MTRCL)

2.02 MTRCL is the Project Proponent and the Permit Holder of the EP of the development of the Project and will assume overall responsibility for the project. Also, an Independent Environmental Checker (IEC) should be employed by MTRCL to audit the results of the EM&A work conducted by Environmental Team.

Environmental Protection Department (EPD)

2.03 EPD is the statutory enforcement body for environmental protection matters in Hong Kong.

Resident Engineer (RE)

2.04 The RE is responsible for overseeing the construction works and for ensuring that the works are undertaken by the Contractor in accordance with the specification and contract requirements. The duties and responsibilities of the ER with respect to EM&A are:

- Monitor the Contractor's compliance with Contract Specifications, including the effective implementation and operation of the environmental mitigation measures;
- Inform the Contractor when action is required to reduce impacts in accordance with the Event and Action Plans;
- Participate in site inspections undertaken by the ET; and
- Co-operate with the ET in providing all the necessary information and assistance for completion of the complaint investigation works.

Independent Environmental Checker (IEC)

2.05 The IEC should advise the ET and RE on environmental issues related to the project. The IEC should audit from an independent viewpoint on the environmental performance during the construction of the project. The IEC should be a person who has relevant professional qualifications in environmental control and at least 7 years' experience in EM&A and environmental management. The duties and responsibilities of the IEC are:

- Review and audit in an independent, objective and professional manner in all aspects of the EM&A programme;
- Validate and confirm the accuracy of monitoring results, appropriateness of monitoring equipment, monitoring locations with reference to the locations of the nearby sensitive receivers, and monitoring procedures;
- Carry out random sample check and audit on monitoring data and sampling procedures, etc;
- Conduct random site inspection;
- Review the effectiveness of environmental mitigation measures and project environmental performance;
- On an as-need basis, verify and certify the environmental acceptability of the construction methodology (both temporary and permanent works), relevant design plans and submissions under the environmental permit. Where necessary, the IEC should agree in consultation with the ET and the Contractor least impact alternative;
- Check complaint cases and the effectiveness of corrective measures;
- Verify EM&A report certified by the ET Leader; and
- Feedback audit results to RE/ET according to the Event/Action Plan.

Environmental Team (ET)

2.06 The ET should conduct the EM&A programme and ensure the Contractor's compliance with the project's environmental performance requirements during construction. The ET should plan, organize and manage the implementation of the EM&A programme and ensure that the EM&A works are undertaken to the required standard.

2.07 The ET should be led and managed by the ET Leader. The ET Leader should have relevant

professional qualifications in environmental control and possess at least 7 years' experience in EM&A. The ET Leader should be responsible for the implementation of the EM&A programmes in accordance with the EM&A requirements. The duties and responsibilities of the ET include:

- Sampling, analysis and statistical evaluation of monitoring parameters;
- Environmental site surveillance;
- Inspection and audit of compliance with environmental protection, and pollution prevention and control regulations;
- Assess the effectiveness of the environmental mitigation measures implemented;
- Monitor compliance with the environmental protection clauses/specifications in the Contract;
- Review construction programme and comment as necessary;
- Review work methodologies which may affect the extent of environmental impact during the construction phase and comment as necessary;
- Complaint investigation, evaluation and identification of corrective measures;
- Liaison with the IEC on all environmental performance matters, and timely submission of all relevant EM&A proforma for IEC's approval; and
- Advice to Contractor on environmental improvement, awareness and enhancement matters etc.

The Contractor

- 2.08 The Contractor should report to the RE. The duties and responsibilities of the Contractor are:
- Comply with the relevant contract conditions and specifications on environmental protection
 - Participate in the site inspections undertaken by the ET;
 - Provide assistance to ET to carry out monitoring;
 - Provide requested information to the ET in the event of any exceedance in the environmental criteria (Action/Limit levels);
 - Submit proposals on mitigation measures in case of exceedances of Action and Limit levels in accordance with the Event / Action Plans; and
 - Cooperate with the ET in providing all the necessary information and assistance for completion of the complaint investigation works. If mitigation measures are required following the investigation, the Contractor should promptly carry out these measures.

SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.09 In accordance with the EP stipulation, the required documents and submission status to EPD are listed in Table 2-1.

Table 2-1 Submission/Set-up Status of the EP Requirements

EP Condition	Submission	Status
2.3	Management Organization of Main Construction Companies	Submitted
2.7	Landscape Plan	Submitted
3.3	Baseline Monitoring Report (TCS00704/14/600/R0010v4)	Submitted
4.2	Internet website	live

- 2.10 Summary of environmental permits, licenses, and relevant notifications on environmental protection for the Project are presented in **Table 2-2**.

Table 2-2 Status of Environmental Licenses and Permits of the Project

Item	Description	License/Permit Status
1	Air Pollution Control (Construction Dust) Regulation	Notified EPD.
2	Chemical Waste Producer Registration - Waste Producers Number	WPN:5213-131-K3099-01 Approved on 14/05/2014
3	Water Pollution Control Ordinance - Discharge License	License no.: WT00019539-2014 Approved on 16/07/2014 Valid to: 31/07/2019
4	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	Account no.: 7019837 Approved on 30/04/2014

Item	Description	License/Permit Status
5	Construction Noise Permit under Noise Control Ordinance	GW-RS0530-16 obtained on 3 June 2016 Valid from 11 June 2016 to 10 Dec 2016 GW-RS0928-16 obtained on 11 August 2016 Valid from 10 September 2016 to 09 March 2017 GW-RS0929-16 obtained on 14 August 2016 Valid from 14 September 2016 to 13 March 2017

CONSTRUCTION PROGRESS

2.11 The construction activities conducted in the Reporting Period are listed in below. Moreover, the master construction program is shown in **Appendix B**.

- ELS Stage 2
- Breakthrough at WAC Station D-wall
- BS installation at new LTS Subway
- ABWF works at new LTS Subway

3 ENVIRONMENTAL IMPACT MONITORING REQUIREMENT

3.01 The ET will implement the EM&A programme in accordance with the requirements in EMAP. Details of the EM&A programme are presented in the following sub-sections.

MONITORING PARAMETERS

3.02 The EM&A impact monitoring program covers the following environmental aspects:

- Air quality; and
- Construction noise

3.03 A summary of the monitoring parameters is presented in *Table 3-1*:

Table 3-1 Summary of the monitoring parameters of EM&A Requirements

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> • 24-hour Total Suspended Particulate (hereinafter ‘24-hour TSP’) • 1-hour TSP monitoring (*)
Construction Noise	<ul style="list-style-type: none"> • A-weighted equivalent continuous sound pressure level (30min) (hereinafter ‘$L_{eq(30min)}$’ during the normal working hours)

Remarks:

(*) *In case 24-hour TSP exceed the air quality criteria to be carried out*

MONITORING LOCATIONS

3.04 According to Sections 2.3 and 3.4 of the EMAP which enclosed in the Project Profile (Register No. PP-472/2012), construction noise and air quality monitoring locations are required to be set up at Hennessy Building and Chiu Hin Mansion. In early May 2014, site visit was conducted to select suitable locations to carry out relevant noise and air monitoring for the EM&A Programme. It was noted that both Hennessy Building and Chiu Hin Mansion are residential buildings and only the 1/F to 2/F of the buildings could be accessed which are commercial premises. It is not possible to set up the monitoring station at upper floors inside the residential apartment which will cause nuisance to the residents. Finally, two locations at lower floor were selected which access were successfully granted by the premises occupiers. The monitoring stations proposed for the Project are summarized in *Table 3-2* and illustrated in *Appendix C*.

Table 3-2 Air and Noise Monitoring Locations

Aspect	Monitoring Location	Location ID	Address	Description
Air Quality	Chiu Hin Mansion	A1	balcony at 1/F of Chiu Hin Mansion	ASR close to the Project site
Construction Noise	Hennessey Building	N1	2/F floor of Hennessey Building	NSR facing to the Project site
	Chiu Hin Mansion	N2	balcony at 1/F of Chiu Hin Mansion	NSR facing to the Project site

MONITORING FREQUENCY AND PERIOD

3.05 The requirements of impact monitoring as stipulated in the EMAP are presented in following.

Air Quality

3.06 Frequency of impact air quality monitoring:

- 24-hour TSP Once every 6 days during course of works.

3.07 In case of non-compliance with the air quality criteria, a more frequent monitoring exercise adopting 1-hour TSP monitoring undertaken when the highest dust impact occurs, as specified in the Event and Action Plan, should be conducted within 24 hours after the result is obtained. This additional monitoring should be continued until excessive dust emission or the deterioration in air quality is rectified.

Construction Noise

- 3.08 One set of $L_{eq(30min)}$ as 6 consecutive $L_{eq(5min)}$ between 0700-1900 hours on normal weekdays and once every week during course of works. If construction work necessary to carry out at other time periods, i.e. restricted time period (19:00 to 07:00 the next morning and whole day on public holidays) (hereinafter referred as “the restricted hours”), 3 consecutive $L_{eq(5min)}$ measurement will be depended on CNP requirements to undertake. Supplementary information for data auditing, statistical results such as L_{10} and L_{90} shall also be obtained for reference.

MONITORING EQUIPMENT

Air Quality Monitoring

- 3.09 The 24-hour TSP shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B (USEPA)*. A direct reading dust meter is used to measure 1-hour TSP air quality, in case of non-compliance of air quality criteria occurred in 24-hour TSP measurement.
- 3.10 The filter paper sample collected in 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory. All equipments to be used for air quality monitoring are listed in **Table 3-3**.

Table 3-3 Air Quality Monitoring Equipment

Equipment	Model
<i>24-hour TSP</i>	
High Volume Air Sampler	TISCH High Volume Air Sampler, HVS Model TE-5170
Calibration Kit	TISCH Model TE-5025A
<i>1- hour TSP</i>	
Portable Dust Meter	TSI Model 8520 DustTrak Aerosol Monitor / Aerocet 531 Handheld Particle Mass Profiler & Counter / Sibata LD-3A Laser Dust Monitor

- 3.11 According to the EMAP, wind data monitoring equipment shall be provided and set up for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET and agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:
- 1) The wind sensors should be installed 10 m above ground so that they are clear of obstructions or turbulence caused by buildings.
 - 2) The wind data should be captured by a data logger. The data shall be downloaded for analysis at least once a month.
 - 3) The wind data monitoring equipment should be re-calibrated at least once every six months.
 - 4) Wind direction should be divided into 16 sectors of 22.5 degrees each.
- 3.12 Although ET was successful granted HVS installation premises, the owners rejected to install wind data monitoring equipment.
- 3.13 In this situation, the ET proposed to adopt the meteorological information from King’s Park Weather Station from the Hong Kong Observatory as the representative wind data. King’s Park Station provided all useful from information such as humidity, rainfall, and air pressure and temperature etc.
- 3.14 Although there are other closer weather stations, King’s Park Station was selected as it is the nearest weather station that measures all the relevant parameters mentioned above. Moreover, the ET has compared the data among the stations, and concluded that there is minimal difference between meteorological data collected at the King’s Park station and other stations.

Construction Noise Monitoring

- 3.15 Sound level meter in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind

speed shall be checked with a portable wind speed meter capable of measuring the wind speed in ms^{-1} . Furthermore, an acoustic calibrator and sound level meter shall be calibrated yearly.

- 3.16 Noise monitoring equipment to be used for monitoring is listed in *Table 3-4*.

Table 3-4 Construction Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	B&K Type 2238/ Rion NL-52
Calibrator	B&K Type 4231/ Rion NC-73
Portable Wind Speed Indicator	Testo Anemometer

MONITORING METHODOLOGY

24-hour TSP

- 3.17 The equipment used for 24-hour TSP measurement is a Tisch Environmental, Inc. Model TE-5170 TSP high volume air sampling system, which complied with USEPA Code of Federal Regulation, Appendix B to Part 50. The High Volume Air Sampler (HVS) consists of the following:
- An anodized aluminum shelter;
 - A 8”x10” stainless steel filter holder;
 - A blower motor assembly;
 - A continuous flow/pressure recorder;
 - A motor speed-voltage control/elapsed time indicator;
 - A 7-day mechanical timer, and
 - A power supply of 220v/50 hz
- 3.18 The HVS is calibrated in accordance with the manufacturer’s instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5028A). The 24-hour TSP monitoring using the HVS is also processed in accordance with the manufacturer’s Operations Manual. The valid calibration certificate of the calibration kit with the certificate of HVS calibrated is shown in *Appendix D*.
- 3.19 24-hour TSP is collected on filters of the HVS and quantified by a local HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd (ALS), upon receipt of the samples. The ET will keep all the sampled 24-hour TSP filters in normal air conditioned room conditions, i.e. 70% HR (Relative Humidity) and 25°C, for six months prior to disposal. HOKLAS-accreditation certificate of ALS Technichem (HK) Pty Ltd (ALS) is provided in *Appendix E*.

Noise

- 3.20 Sound level meter complied with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications, as recommended in Technical Memorandum (TM) issued under the Noise Control Ordinance (NCO). The valid of calibration certificates including sound level meter and an acoustic were shown in *Appendix D*.
- 3.21 The noise measurement is performed with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (L_{eq}). $L_{eq(30min)}$ in six consecutive $L_{eq(5min)}$ measurements were used as the monitoring parameter.
- 3.22 During monitoring, the sound level meter mounted at the monitoring locations and oriented such that the microphone pointed to the site with the microphone facing perpendicular to the line of sight. The windshield was fitted for the measurement. For the monitoring, N1 and N2 are conducted 1 m from the exterior of the building façade.
- 3.23 Prior construction noise measurement, the accuracy of the sound level meter checked using an acoustic calibrator generating a known sound pressure level at a known frequency. The calibration level from before and after the noise measurement agrees to within 1.0dB.

DERIVATION OF ACTION/LIMIT (A/L) LEVELS

- 3.24 The baseline results form the basis for determining the environmental acceptance criteria for the impact monitoring. According to EMAP, the air quality and construction noise criteria were set up, namely Action and Limit levels are listed in *Tables 3-5* and *3-6*.

Table 3-5 Action and Limit Levels for Air Quality Monitoring

Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
A1	290	162	500	260

Table 3-6 Action and Limit Levels for Construction Noise

Monitoring Station	0700-1900 hours on normal weekdays	
	Action Level	Limit Level
N1 and N2	When one documented complaint is received	75 dB(A)

Note: If works are to be carried out during restricted hours, the conditions stipulated in the construction noise permit issued by the NCA have to be followed.

- 3.25 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in *Appendix F*.

DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.26 The all monitoring data were handled by the ET's in-house data recording and management system.
- 3.27 The monitoring data recorded in the equipment were downloaded directly from the equipment at the end of each monitoring day. The downloaded monitoring data were input into a computerized database properly maintained by the ET. The laboratory results were input directly into the computerized database and checked by personnel other than those who input the data.
- 3.28 For monitoring parameters that require laboratory analysis, the local laboratory shall follow the QA/QC requirements as set out under the HOKLAS scheme for the relevant laboratory tests.

4 MONITORING RESULTS

4.01 The impact air quality and construction noise monitoring schedule is presented in *Appendix G* and the monitoring results are summarized in the following sub-sections.

24-HOUR TSP AIR QUALITY MONITORING RESULTS

4.02 In the Reporting Period, **5** occasions of 24-hours TSP monitoring were carried out at the proposed location A1 and the monitoring results are summarized in *Table 4-1*. The detailed 24-hour TSP monitoring data are presented in *Appendix H* and the relevant graphical plots are shown in *Appendix I*.

Table 4-1 Summary of 24-hour TSP Monitoring Results – A1

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	Action Level	Limit Level
4-Nov-16	82	162	260
10-Nov-16	58		
16-Nov-16	82		
22-Nov-16	36		
28-Nov-16	71		
Average (Range)	66 (36 – 82)		

4.03 As shown in *Table 4-1*, 24-hour TSP monitoring results are fluctuated below Action/ Limit Levels.

NOISE MONITORING RESULTS

4.04 In the Reporting Period, **10** occasions noise measurement were conducted at N1 and N2. The sound level meter was set in 1m from the exterior of the building façade at N1 and N2. Therefore, no façade correction (+3dB(A)) is added according to acoustical principles and EPD guidelines. The noise measurement results at N1 and N2 are listed in *Tables 4-2* and *4-3*. The relevant graphical plots are shown in *Appendix I*.

Table 4-2 Noise Monitoring Results of N1 (2/F floor of Hennessey Building), dB(A)

Date	Start Time	1st Leq5	2nd Leq5	3rd Leq5	4th Leq5	5th Leq5	6th Leq5	L _{eq30min}
3-Nov-16	15:49	70.8	71.5	72.1	71.5	70.7	71.5	71
11-Nov-16	9:47	72.0	71.1	70.8	71.6	70.9	71.7	71
17-Nov-16	11:21	66.8	67.2	67.5	67.8	67.9	68.4	68
24-Nov-16	11:04	67.4	67.0	68.0	67.5	68.0	68.7	68
29-Nov-16	13:11	68.1	67.5	68.3	67.8	68.1	67.3	68
Limit Level of Construction Noise		75 dB(A)						

Table 4-3 Noise Monitoring Results of N2 (balcony at 1/F of Chiu Hin Mansion), dB(A)

Date	Start Time	1st Leq5	2nd Leq5	3rd Leq5	4th Leq5	5th Leq5	6th Leq5	L _{eq30min}
3-Nov-16	15:07	68.4	67.3	69.3	69.5	68.5	68.0	69
11-Nov-16	10:31	67.7	69.2	68.7	69.4	68.6	67.5	69
17-Nov-16	13:01	69.1	69.4	67.2	68.0	68.0	67.0	68
24-Nov-16	13:07	69.5	68.9	67.3	68.3	68.2	67.7	68
29-Nov-16	14:17	68.7	69.8	67.5	68.8	67.9	68.5	69
Limit Level of Construction Noise		75 dB(A)						

4.05 As shown in Tables 4-2 and 4-3, no noise measurement exceedance was recorded at both N1 and N2. Furthermore, there is no noise complaint (Action Level exceedance) received by the MTRCL and Contractor or EPD in the Reporting Period. The meteorological data during the impact monitoring days are shown in *Appendix J*.

5 WASTE MANAGEMENT

GENERAL WASTE MANAGEMENT

5.01 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

RECORDS OF WASTE QUANTITIES

5.02 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

5.03 The quantities of waste for disposal in this Reporting Period are summarized in *Tables 5-1* and *5-2* and the Monthly Summary Waste Flow Table is shown in *Appendix K*.

Table 5-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
Total C&D Materials (Inert) ('000m ³)	0.61515	-
Reused in this Contract (Inert) ('000m ³)	0	-
Reused in other Projects (Inert) ('000m ³)	0	-
Disposal as Public Fill (Inert) ('000m ³)	0.61515	TKO 137

Table 5-2 Summary of Quantities of Non-Inert C&D Wastes

Type of Waste	Quantity	Disposal Location
Recycled Metal ('000m ³)	0	-
Recycled Paper / Cardboard Packing ('000m ³)	0	-
Recycled Plastic ('000m ³)	0	-
Chemical Wastes ('000m ³ /L)	0	-
General Refuses ('000m ³)	0	-

5.04 In the Reporting Period, effluent generated from the Project was discharged in accordance with the Wastewater Discharge License.

5.05 Moreover, it is reminded that C&D materials would be reused on-site as far as practicable.

6 SITE INSPECTION

6.01 According to the EMAP, the environmental site inspection shall be formulation by ET Leader. Weekly environmental site inspections should carry out to confirm the environmental performance.

FINDINGS / DEFICIENCIES DURING THE REPORTING MONTH

6.02 During the Reporting Period, **Five (5)** occasions of weekly site inspections to evaluate site environmental performance was carried out by the RE, ET and the Contractor on **3, 11, 17, 24 and 29 November 2016** and the IEC was joined the site inspection on **29 November 2016**.

6.03 No non-compliance was noted. However, four (4) observations and one (1) reminder were recorded by the ET. The findings / deficiencies observed during the weekly site inspections are listed in **Table 6-1**.

Table 6-1 Site Observations

Date	Findings / Deficiencies	Follow-Up Status
27 October 2016	<ul style="list-style-type: none"> • Construction materials were observed near tree protection zone. The contractor was advised to remove it as soon as possible. • The contractor was reminded to maintain the AquaSed regularly. 	<ul style="list-style-type: none"> • Construction materials were removed. Last observation closed. • Not required for reminder.
3 November 2016	<ul style="list-style-type: none"> • No adverse environmental issue was observed. 	<ul style="list-style-type: none"> • Nil
11 November 2016	<ul style="list-style-type: none"> • Accumulation of sediment was observed. The contractor was advised to dispose the sediment in sedimentation tank regularly. • Chemical containers were observed on the ground. The contractor was advised to place chemical containers inside drip tray. 	<ul style="list-style-type: none"> • A sedimentation tank was maintained. Last observation closed. • Chemical containers were removed from site. Last observation closed.
17 November 2016	<ul style="list-style-type: none"> • Discharge of wastewater was observed. The contractor was advised to treat the wastewater by AquaSed before discharge. 	<ul style="list-style-type: none"> • To be followed.
24 November 2016	<ul style="list-style-type: none"> • The contractor was advised to dispose the empty cement bags regularly. 	<ul style="list-style-type: none"> • Not required for reminder.
29 November 2016	<ul style="list-style-type: none"> • Chemical containers were observed on bare ground. The contractor was advised to place chemical containers inside drip tray. 	<ul style="list-style-type: none"> • To be followed in next reporting period.

6.04 It is reported that the transplanted tree TR-02 for this project was collapsed due to typhoon signal No. 8 HAIMA on 22 October 2016 and the tree has been subsequently removed. Further follow-up action will be made after an agreement is reached with Leisure and Cultural Services Department (LCSD).

6.05 No site inspection was undertaken by external parties i.e. EPD in this Reporting Month.

7 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

7.01 For the Project, no environmental complaint, summons and prosecution was received in the Reporting Period. The statistical summary table of environmental complaint is presented in *Tables 7-1, 7-2 and 7-3.*

Table 7-1 Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics					
	Frequency	Cumulative	Complaint Nature			
			Air	Noise	Water	Others
28 Aug 2014 – 31 October 2016	0	0	NA	NA	NA	NA
1– 30 November 2016	0	0	NA	NA	NA	NA

Table 7-2 Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics					
	Frequency	Cumulative	Air	Noise	Water	Others
28 Aug 2014 – 31 October 2016	0	0	NA	NA	NA	NA
1– 30 November 2016	0	0	NA	NA	NA	NA

Table 7-3 Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics					
	Frequency	Cumulative	Air	Noise	Water	Others
28 Aug 2014 – 31 October 2016	0	0	NA	NA	NA	NA
1– 30 November 2016	0	0	NA	NA	NA	NA

8 IMPLEMENTATION STATUS OF MITIGATION MEASURES

GENERAL REQUIREMENTS

- 8.01 The environmental mitigation measures that recommended in the Implementation Schedule for Environmental Mitigation Measures (ISEMM) in the EMAP covered the issues of dust, noise, water and waste and they are summarized presented in *Appendix L*.
- 8.02 The Works under the Project shall be implementing the required environmental mitigation measures according to the EMAP as subject to the site condition. Environmental mitigation measures generally to be implemented by the Contractor is listed in *Table 8-1*.

Table 8-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Air Quality	<ul style="list-style-type: none"> • Regular watering to reduce dust emissions from all exposed site surface, particularly during dry weather; • Frequent watering for particularly dusty construction areas and areas close to air sensitive receivers; • Cover all excavated or stockpile of dusty material by impervious sheeting or sprayed with water to maintain the entire surface wet; • Public areas around the site entrance/exit had been kept clean and free from dust; and • Tarpaulin covering of any dusty materials on a vehicle leaving the site.
Noise	<ul style="list-style-type: none"> • Good site practices to limit noise emissions at the sources; • Use of quiet plant and working methods; • Use of site hoarding or other mass materials as noise barrier to screen the working site; • Use of shrouds/temporary noise barriers to screen noise from relatively static PMEs; and • Limiting as use one construction plant within worksite, where practicable.
Water Quality	<ul style="list-style-type: none"> • Wastewater were appropriately treated by treatment facilities; • Drainage channels were provided to convey run-off into the treatment facilities; and • Drainage systems were regularly and adequately maintained.
Waste and Chemical Management	<ul style="list-style-type: none"> • Excavated material should be reused on site as far as possible to minimize off-site disposal. Scrap metals or abandoned equipment should be recycled if possible; • Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner; • The Contractor should adopt a trip ticket system for the disposal of C&D materials to any designed public filling facility and/or landfill; and • Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.
Landscape and Visual	<ul style="list-style-type: none"> • Clear demarcation of works area to prevent damages to existing trees in close proximity; • Protection of all trees planned to be retained onsite; • Preserving all affected trees by transplanting where practical. Tree transplanting application and tree removal application shall be submitted for approval in accordance with ETWB TCW 3/2006; and • Screening of construction works by hoardings/noise barriers around Works area in visually unobtrusive colors.
General	<ul style="list-style-type: none"> • The site was generally kept tidy and clean.

TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

8.03 Construction activities as undertaken in the coming month for the Project lists below:

- ELS Stage 2
- RC for subway at Stage 2
- Breakthrough of H15 D-wall
- BS installation at new LTS subway
- ABFW at new LTS subway

KEY ISSUES FOR THE COMING MONTH

8.04 Key issues to be considered in the coming month of the Project include:

- Implementation of dust suppression measures at all times;
- Potential wastewater quality impact due to surface runoff;
- Potential fugitive dust quality impact due from the dry/loose/exposure soil surface/dusty material;
- Disposal of empty engine oil containers within site area;
- Ensure dust suppression measures are implemented properly;
- Silt removal facilities should be regularly maintained;
- Management of chemical wastes;
- Discharge of site effluent and stockpiling or disposal of materials at this area are prohibited;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures

8.05 In addition, mosquito control measures should be continued to prevent mosquito breeding on site.

9 CONCLUSIONS AND RECOMMENDATIONS

CONCLUSION


- 9.01 This is the 27th monthly EM&A report presenting the monitoring results and inspection findings in the Reporting Period from 1 to 30 November 2016.
- 9.02 In the Reporting Period, **five (5)** occasions of 24-hours TSP monitoring were conducted at A1. The monitoring results are all below the Action/ Limit Level. No Notifications of Exceedances (NOEs) or the associated corrective actions were therefore issued.
- 9.03 In the Reporting Period, total of **ten (10)** occasions of noise measurement were conducted at N1 and N2 and no exceedance were recorded.
- 9.04 No environmental complaint, notification of summons or successful prosecution was received in the Reporting Period.
- 9.05 **Five (5)** occasions of weekly site inspections to evaluate site environmental performance was carried out by the RE, ET and the Contractor on **3, 11, 17, 24 and 29 November 2016** and the IEC was joined the site inspection on **29 November 2016**. No non-compliance was noted but four (4) observations and one (1) reminder were recorded by the ET.
- 9.06 It is reported that the transplanted tree TR-02 for this project was collapsed due to typhoon signal No. 8 HAIMA on 22 October 2016 and the tree has been subsequently removed. Further follow-up action will be made after an agreement is reached with Leisure and Cultural Services Department (LCSD).
- 9.07 In the Reporting Period, no site inspection was undertaken by external parties i.e. EPD.

RECOMMENDATIONS

- 9.08 Construction noise is the key environmental issue during construction work of the Project as there are residential buildings nearby. Noise mitigation measures should be fully implemented in accordance with the EM&A requirement.
- 9.09 Also, special attention should be paid on the potential construction dust impact as the construction site is located near the residential area. The Contractor should fully implement the construction dust mitigation measures properly.
- 9.10 The Contractor should also prevent muddy water and other water pollutants via site surface water runoff get into public areas. Any discharge water should be strictly complied with wastewater discharge license requirement. As a reminder, water quality mitigation measures should be properly implemented in accordance with the EM&A requirement.
- 9.11 As a reminder, the Contractor should be regular checking and maintenance wastewater treatment facilities ensure compliance with the currently Discharge License stipulation. A warning sign should be provided all the retained trees as remind the workers prevent scratch the trees. In addition, mosquito control should be kept to prevent mosquito breeding on site.

Appendix A
Project Site Layout Plan

C:\ProgramData\Bentley\MicroStation\18\USELECT\series\WorkSpace\System\pctrig\WTR_PDF_BW_COL_300DP.plt
 PLOT DRW: 20/06/2012 16:50:06
 MODELNAME: NEX1050_2.7A_0010.dgn
 FILENAME: NEX1050_2.7A_0010.dgn

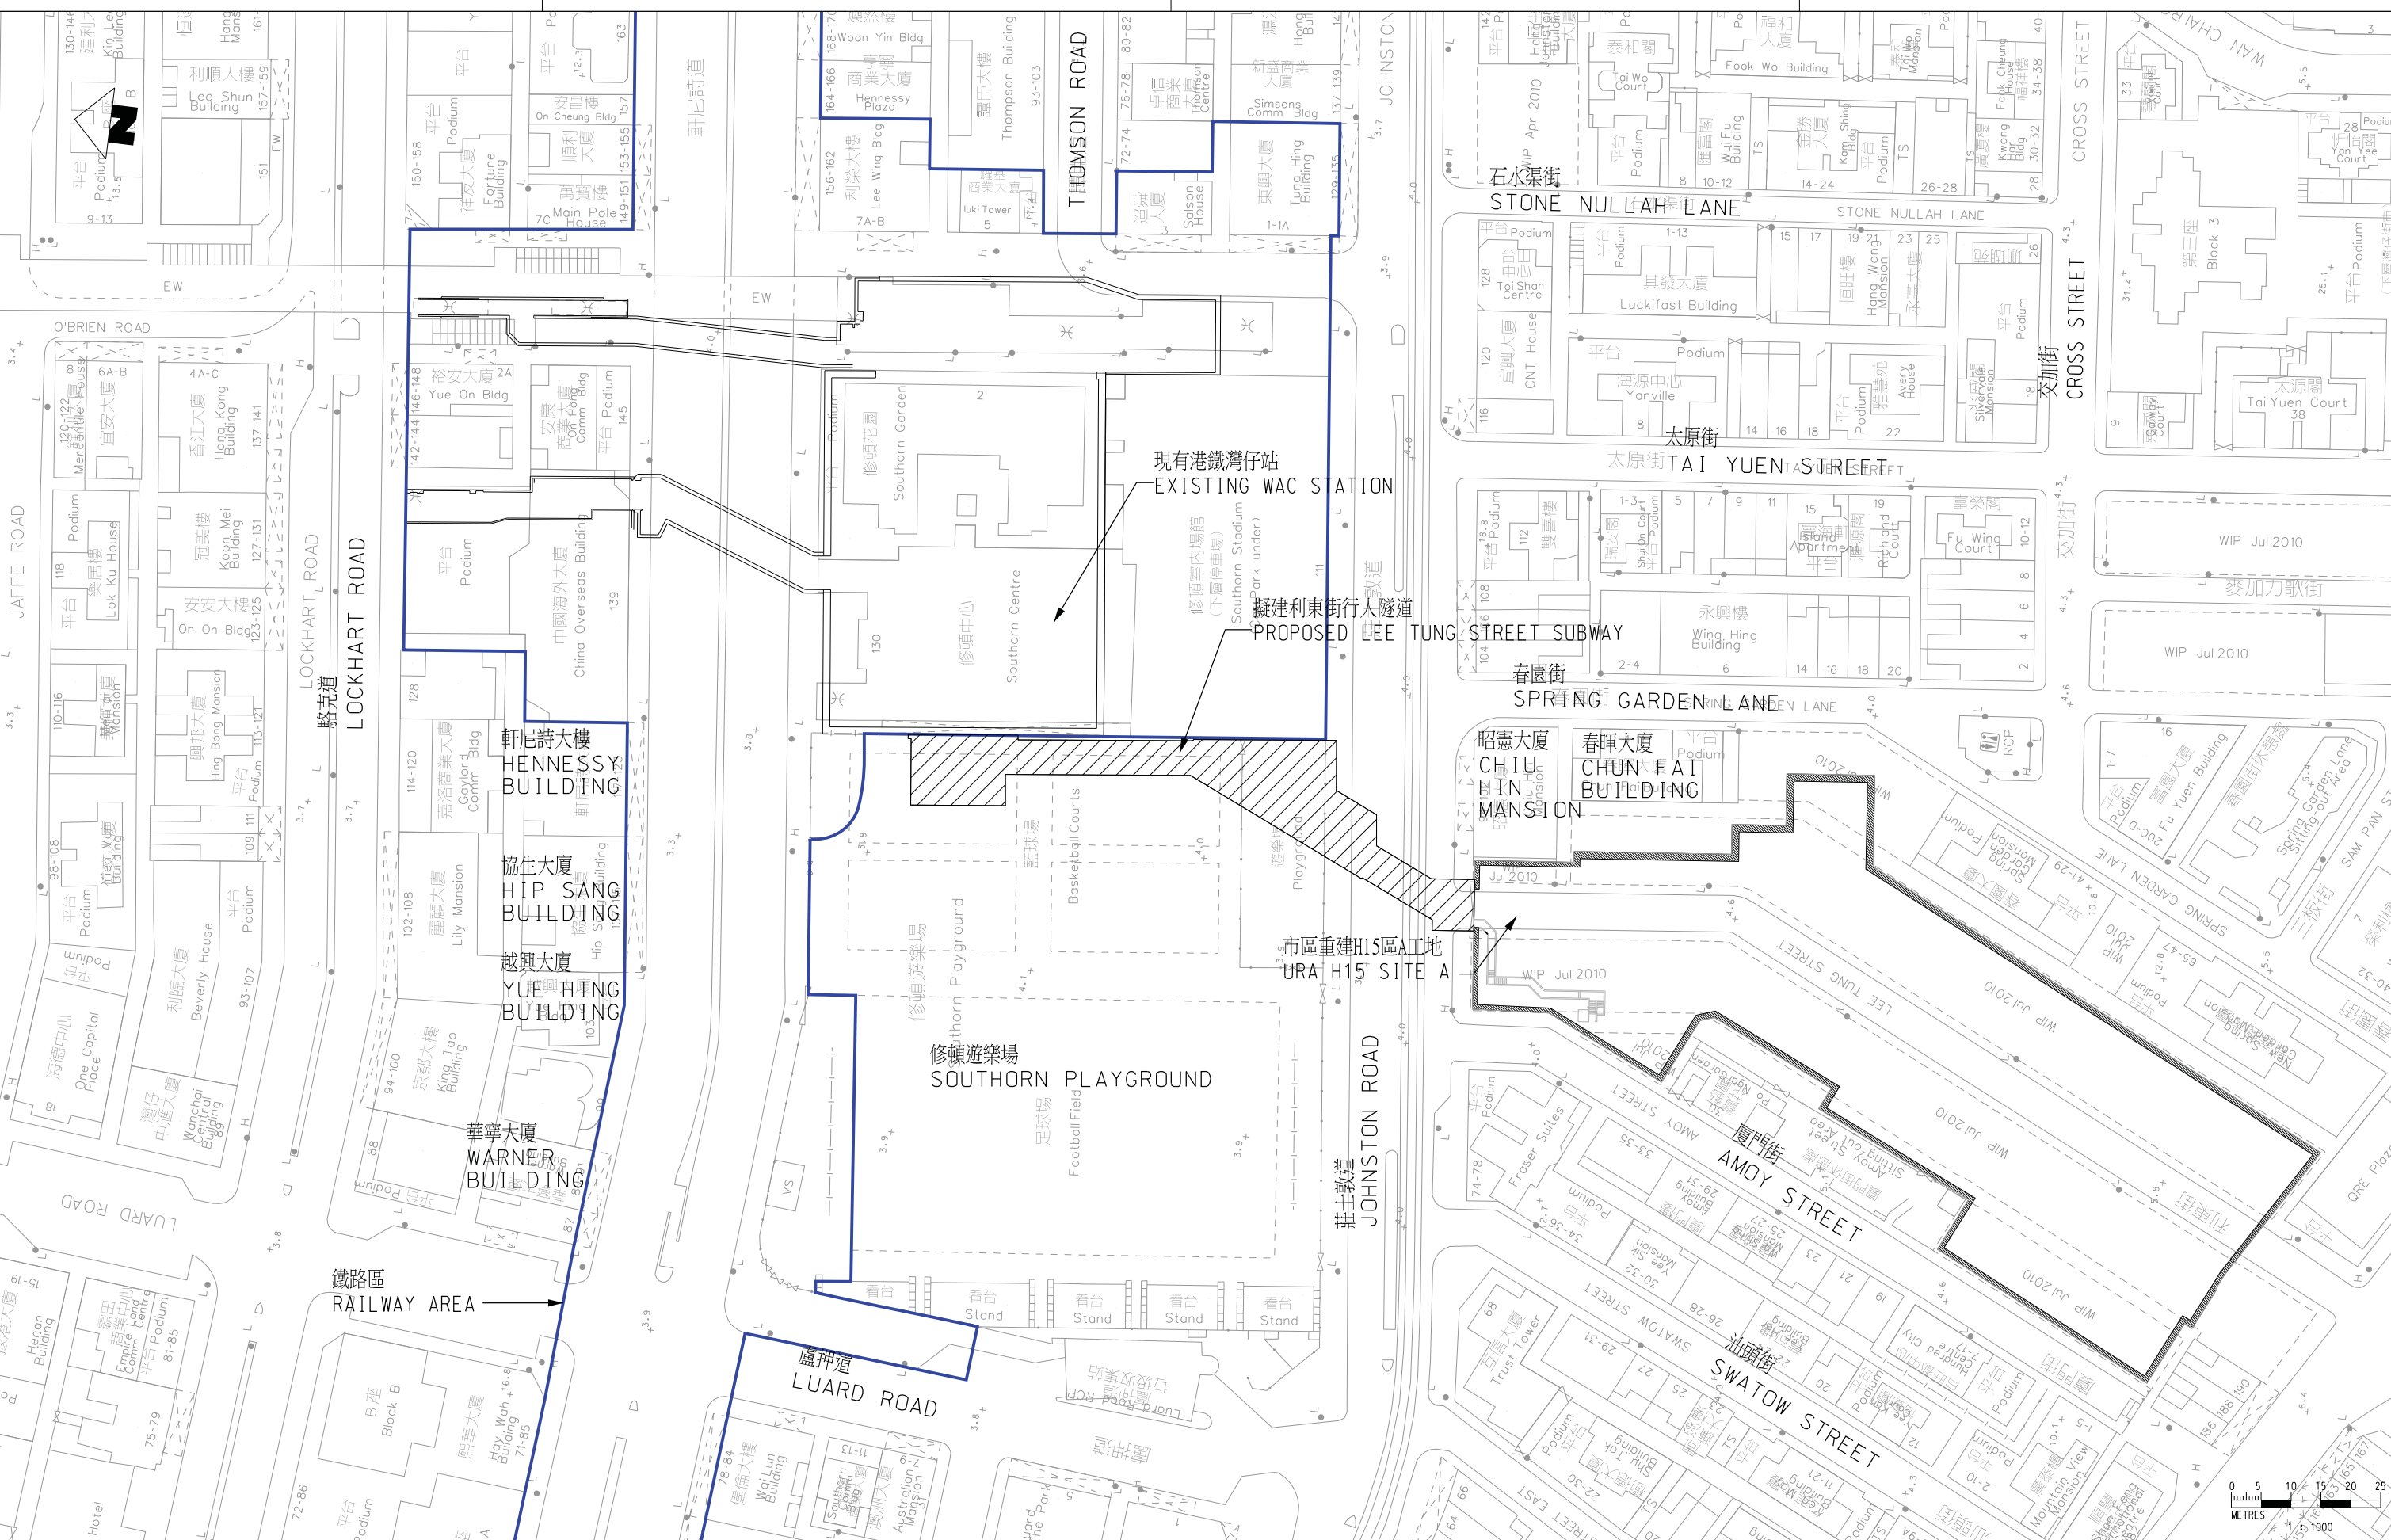

REV	DESCRIPTION	BY	DATE	APPROVED	REV	DESCRIPTION	BY	DATE	APPROVED
D	GENERAL REVISION		16MAY12	AFK	HD				
C	GENERAL REVISION		12AUG11	AFK	HD				
B	GENERAL REVISION		18JUL11	AFK	HD				
A	PROJECT PROFILE		04MAY11	AFK	HD				

DRAWN	HO
DESIGNED	BW
CHECKED	BL
APPROVED	AFK
DATE	04MAY2011

ORIGINATOR
MTR
Mott MacDonald


CADD REF. NEX1050_2.7A_0010.dgn

TITLE
CONSULTANCY AGREEMENT NO. NEX/1050
DETAILED DESIGN FOR LEE TUNG STREET SUBWAY
 SITE LOCATION PLAN
 施工位置圖

SCALE 1:1000 (A3) DRAWING NO. NEX1050/2.7A/001 REV. D

Appendix B

**Organization of the Project
and
Master Construction Programme**

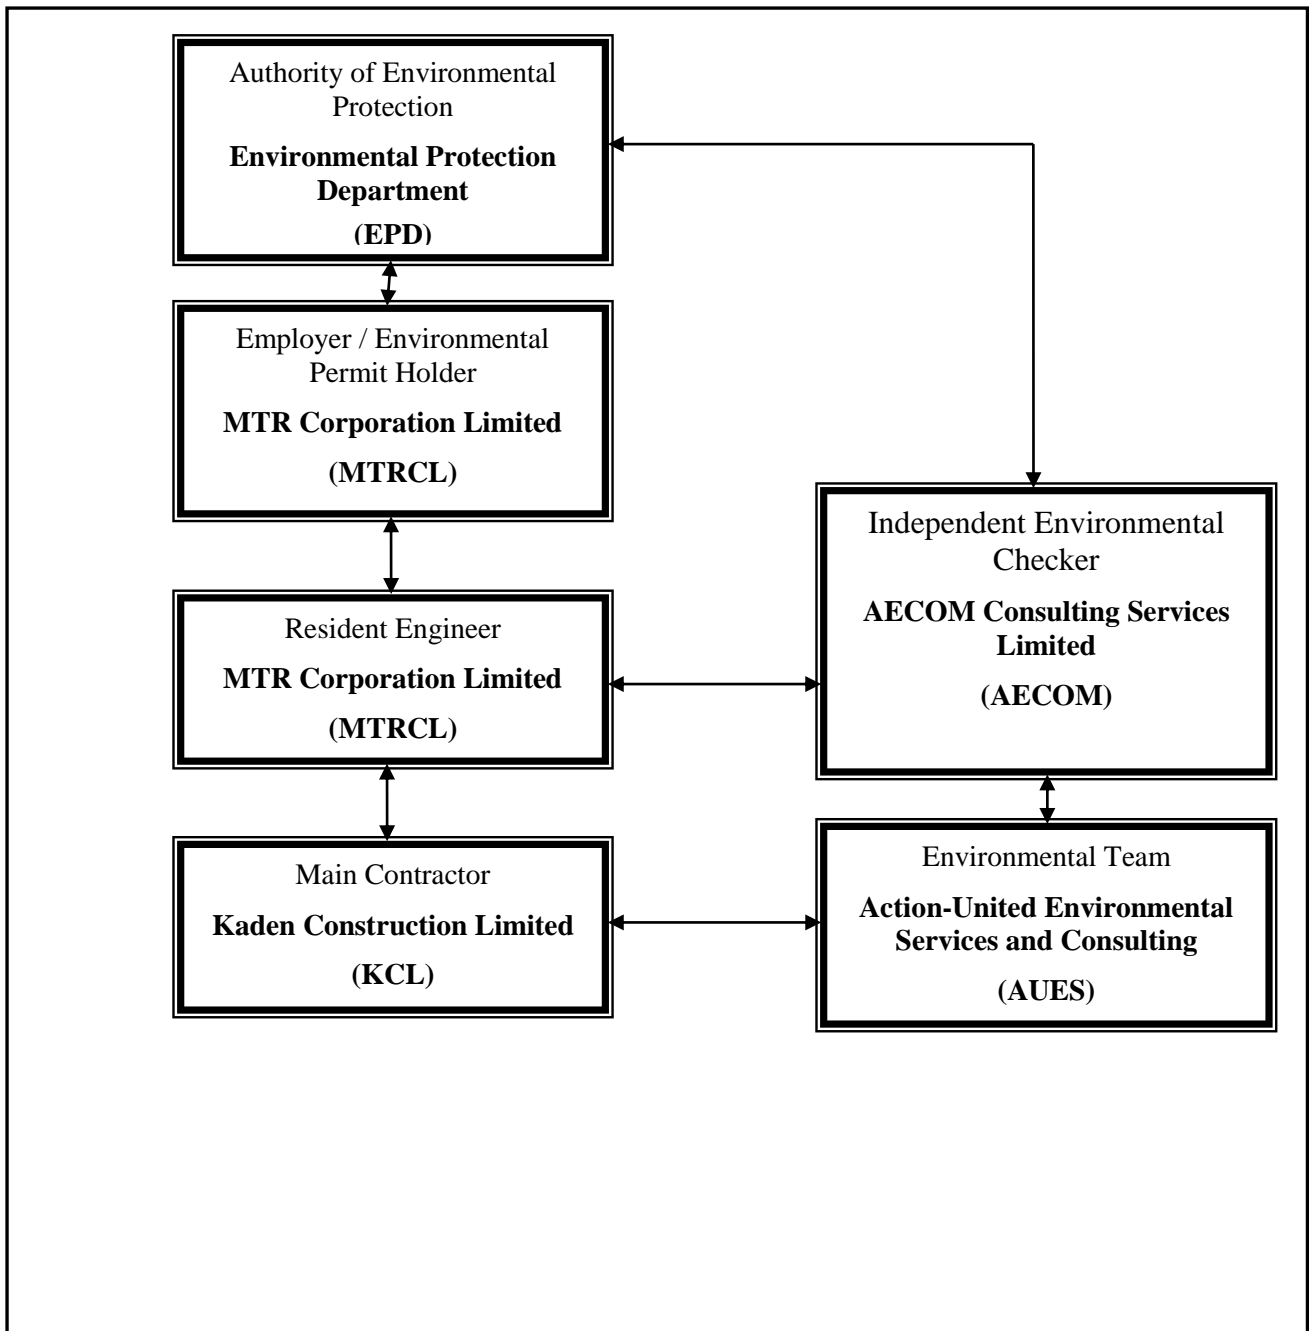

Contact Details of Key Personnel for the Project

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
MTRCL	Resident Engineer	Mr. Raymond Lee	3547 0002	3547 0090
AECOM	Independent Environmental Checker	Mr. Y. W. Fung	3922 9366	3922 9797
KCL	Project Manager	Mr. Vincent, Kwan Chun Yin	9833 1313	2770 4278
KCL	Site Agent	Mr. Chan Kam Chuen	6462 8910	2770 4278
KCL	Environmental Officer	Ms. Ricci Poon Wai Tin	9533 1115	2770 4278
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Mr. Ben Tam	2959 6059	2959 6079
AUES	Assistant Environmental Consultant	Mr. Martin Li	2959 6059	2959 6079

Legend:

MTRCL (Employer) – MTR Corporation Limited

MTRCL (Resident Engineer) – MTR Corporation Limited

KCL (Main Contractor) – Kaden Construction Limited

AECOM (IEC) – AECOM Consulting Services Limited

AUES (ET) – Action-United Environmental Services & Consulting

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)														
Key Dates																							
Commencement and Completion																							
KD.COMM	Commencement of the Works (14-Apr'14)	0	14-Apr-14 A		14-Apr-14				[Gantt Chart]														
KD.COMP	Completion of the Whole of the Works, No.Cal.Wk. 150 (26-Feb'17)	0		28-Jul-18*		28-Jul-18	-517	0	[Gantt Chart]														
Specified Parts of the Works																							
KD.2A	2A - SBC Complete backfill, resurfacing, fencing, utilities, lighting and return to LCSD (2E	0		11-Aug-15 A		02-Jul-15			[Gantt Chart]														
KD.2B	2B - Complete all works at the 2 new Shop Kiosks and hand over to the Employer (1-Ma	0		16-Sep-17*		16-Sep-17	-503	315	[Gantt Chart]														
Programme Data / Interface Key Dates																							
INF.AFC	Interface Access for AFC, C&C DC in new AFC Audit Room inside WAC, Concourse Le	0	31-Oct-16*		31-Oct-16		119	636	[Gantt Chart]														
INF.H15	Interface Access for Contract H15, All Levels, No.Cal.Wk. 120 (31-Jul'16)	0	01-Jul-17*		01-Jul-17		-124	393	[Gantt Chart]														
INF.SAMS	Interface Access for SAMS, Comms, MCS to All Areas, All Levels and Locations (10-Oct*	0	07-Sep-17*		07-Sep-17		-192	325	[Gantt Chart]														
Site Area Possession and Return Dates																							
Site Area Possession Date																							
WAP.W1	WorksArea 6593.W1, Within 3 months from commencement of works (14-Jul'14)	0	14-Jul-14 A		14-Jul-14				[Gantt Chart]														
WAP.W2	WorksArea 6593.W2, Within 9 months from commencement of works (14-Jan'15)	0	31-Oct-16*		31-Oct-16		119	636	[Gantt Chart]														
WAP.W3	WorksArea 6593.W3, No later than 1 month after completion of reinstatement works a	0	05-Sep-17		05-Sep-17		-238	0	[Gantt Chart]														
Site Area Return Date																							
WAR.W1	WorksArea 6593.W1, Within 36 months from commencement of works (14-Apr'17)	0		11-Aug-17*		11-Aug-17	-238	0	[Gantt Chart]														
WAR.W2	WorksArea 6593.W2, Within 36 months from commencement of works (14-Apr'17)	0		22-Mar-17*		22-Mar-17	-24	494	[Gantt Chart]														
WAR.W3	WorksArea 6593.W3, Within 2 months after possession date of WorksArea 6593.W3	0		22-Oct-17		22-Oct-17	-238	279	[Gantt Chart]														
Milestone Schedule																							
Milestones A																							
MS.A01	A1 Approval of Preliminary Master Program, ICE, TTA, ELS & Temporary decking (3-Aug	0		21-Oct-14 A		02-Aug-14			[Gantt Chart]														
MS.A02	A2 Approval of Design of Mined Tunnel ESS; Hoarding phase/plan; TW under TramTrac	0		01-Nov-14 A		29-Jul-15			[Gantt Chart]														
MS.A03	A3 Satisfactory Implementation of Specified Plans (25-Jan'15)	0		24-Jan-15 A		31-Mar-15			[Gantt Chart]														
MS.A04	A4 Approval of excavation method under Tram Track; Satisfactory Implementation of PV	0		02-May-15 A		07-Jul-15			[Gantt Chart]														
MS.A05	A5 Approval of WAC D-wall demolition; Satisfactory Implementation of Specified Plans (2	0		31-Oct-16		31-Oct-16	119	636	[Gantt Chart]														
MS.A06	A6 Satisfactory Implementation of PMS (1-Nov'15)	0		30-Sep-15 A		30-Sep-15			[Gantt Chart]														
MS.A07	A7 Satisfactory Implementation of Specified Plans (31-Jan'16)	0		30-Jan-16 A		29-Feb-16			[Gantt Chart]														
MS.A08	A8 AIP for T&C of BS and ABWF works; Satisfactory Implementation of PMS (1-May'16)	0		26-Sep-17		26-Sep-17	-212	305	[Gantt Chart]														
MS.A09	A9 Satisfactory Implementation of Specified Plans (31-Jul'16)	0		31-Oct-16		31-Oct-16	119	636	[Gantt Chart]														
MS.A10	A10 AIP of Draft O&M manual and Draft As-built Drawings; Satisfactory Implementation	0		03-Apr-18		03-Apr-18	-401	116	[Gantt Chart]														
MS.A11	A11 Approval of O&M manual and As-built drawings for the Works (26-Feb'17)	0		28-Jul-18		28-Jul-18	-517	0	[Gantt Chart]														
Milestones B																							
MS.B01	B1 Excavate to +2.5 of Southern Basketball Court & Children's Play Area - Cofferdam co	0		01-Nov-14 A		01-Nov-14			[Gantt Chart]														
MS.B02	B2 SBC Excavation satisfactorily completed & Children's Play Area Excavation has reach	0		24-Jan-15 A		31-Mar-15			[Gantt Chart]														
MS.B03	B3 SBC Roof slab RC, JnR NFP & EBC 67% cofferdam Tram Track support 10%, JnR	0		29-Apr-15 A		23-May-15			[Gantt Chart]														
MS.B04	B4 SBC return, NBC Site entry formed, CPA RC base slab, JnR NFP & EBC Cofferdam	0		11-Aug-15 A		25-Aug-15			[Gantt Chart]														
MS.B05	B5 NBC cofferdam complete, CPA RC & vent shaft 1.2m above ground complete, Tram	0		09-Nov-16		09-Nov-16	109	626	[Gantt Chart]														
MS.B06	B6 NBC Excavation to formation complete, JnR All Carriageways & Footpaths & Tram Ti	0		07-Jan-17		07-Jan-17	50	567	[Gantt Chart]														
MS.B07	B7 NBC RC roof slab complete, JnR CW & FP & TT RC construction except temp openi	0		05-Apr-17		05-Apr-17	-38	479	[Gantt Chart]														
MS.B08	B8 ABWF Degree 1 achieved, NBC All reinstatement complete, Opening through H15 D	0		06-Jul-17		06-Jul-17	-130	387	[Gantt Chart]														
MS.B09	B9 ABWF Degree 3 achieved, All road reinstatement in Johnston Road & Hennessy Roa	0		07-Sep-17		07-Sep-17	-192	325	[Gantt Chart]														
MS.B10	B10 All works in Cost Centre B satisfactorily completed (26-Feb'17)	0		27-Dec-17		27-Dec-17	-303	214	[Gantt Chart]														
Milestones C																							
MS.C01	C1 AIP BS detail design, suppliers & model types of major BS equipment & materials (2-l	0		01-Nov-14 A		01-Nov-14			[Gantt Chart]														
MS.C02	C2 AIP BS shop drawings (25-Jan'15)	0		23-Jan-15 A		31-Mar-15			[Gantt Chart]														

- █ Actual Level of Effort
- █ Critical Remaining ...
- █ Primary Baseline
- ◆ Baseline Milestone
- █ Actual Work
- ◆ Milestone
- █ Remaining Work

**Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)**

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)												
MS.C03	C3 Order all BS equipment and materials (3-May'15)	0		02-May-15 A		01-Jun-15			[Gantt Chart Data]												
MS.C04	C4 Complete all factory acceptance testings (29-Nov'15)	0		28-Nov-15 A		31-Mar-16			[Gantt Chart Data]												
MS.C05	C5 Complete all delivery to site for ECS plant room (31-Jul'16)	0		09-Nov-16		09-Nov-16	109	626	[Gantt Chart Data]												
MS.C06	C6 Complete all installation, T&C for New Subway (4-Dec'16)	0		20-Oct-17		20-Oct-17	-235	282	[Gantt Chart Data]												
MS.C07	C7 Complete and pass all statutory inspections, Operations Team (26-Feb'17)	0		12-Jun-18		12-Jun-18	-471	46	[Gantt Chart Data]												
Milestones D																					
MS.D01	D1 New AFC Audit Room construction completed, including (3-May'15)	0		31-Oct-16		31-Oct-16	119	405	[Gantt Chart Data]												
MS.D02	D2 Old AFC Audit Room and Maxim's/ Circle K kiosks demolished (31-Jan'16)	0		26-Jun-17		26-Jun-17	-120	166	[Gantt Chart Data]												
MS.D03	D3 Breakthrough into WAC (31-Jul'16)	0		11-Nov-17		11-Nov-17	-258	28	[Gantt Chart Data]												
MS.D04	D4 All works in Cost Centre D satisfactorily completed (28-Aug'16)	0		09-Dec-17		09-Dec-17	-286	231	[Gantt Chart Data]												
Milestones E																					
MS.E01	E1- AFC gates and barrier relocation works completed (3-Jan'16)	0		18-Apr-17		18-Apr-17	-51	466	[Gantt Chart Data]												
MS.E02	E2- All structural A&A works for TIM completed (30-Oct'16)	0		29-Jan-18		29-Jan-18	-337	180	[Gantt Chart Data]												
MS.E03	E3- All works in milestone E completed (26-Feb'17)	0		28-May-18		28-May-18	-456	61	[Gantt Chart Data]												
A: Preliminaries and General Items																					
Cost Centre A- Milestone Schedules																					
A1 Approval of Preliminary Master Program, ICE, TTA, ELS & Temporary decking (3-Aug'14)																					
A01_0010	Approval of Preliminary Master Program (3-Aug'14)	0		21-Oct-14 A		02-Aug-14			[Gantt Chart Data]												
A01_0020	Approval of Specified Plans (3-Aug'14)	0		01-Aug-14 A		01-Aug-14			[Gantt Chart Data]												
A01_0030	Approval of Independent Checking Engineer (3-Aug'14)	0		01-Aug-14 A		01-Aug-14			[Gantt Chart Data]												
A01_0040	Approval of the TTM Scheme by the Relevant Authorities (3-Aug'14)	0		27-Jun-14 A		27-Jun-14			[Gantt Chart Data]												
A01_0050	Approval for the design of ELS systems for cofferdams & temporary decking (3-Aug'14)	0		03-Mar-15 A		01-Aug-14			[Gantt Chart Data]												
A2 Approval Design of Mined Tunnel ESS; Hoarding phase/plan; QP, SAP, PMR, H&SP, EMP (2-Nov'14)																					
A02_0010	Approval for the design of excavation support systems of the mined tunnel section (2-Nov'14)	0		16-Jan-15 A		01-Nov-14			[Gantt Chart Data]												
A02_0020	Approval of all phasing plans & hoarding arrangements (2-Nov'14)	0		28-Oct-14 A		28-Oct-14			[Gantt Chart Data]												
A02_0030	Approval of all method statements for Part B works (2-Nov'14)	0		30-Oct-14 A		30-Oct-14			[Gantt Chart Data]												
A02_0040	Engineer's confirmation of satisfactory implementation of Quality Plan (2-Nov'14)	0		01-Nov-14 A		01-Nov-14			[Gantt Chart Data]												
A02_0050	Engineer's confirmation of satisfactory implementation of System Assurance Plan (2-Nov'14)	0		01-Nov-14 A		01-Nov-14			[Gantt Chart Data]												
A02_0060	Engineer's confirmation of satisfactory implementation of Programming Management Sy.	0		01-Nov-14 A		01-Nov-14			[Gantt Chart Data]												
A02_0070	Engineer's confirmation of satisfactory implementation of Health & Safety Plan (2-Nov'14)	0		01-Nov-14 A		01-Nov-14			[Gantt Chart Data]												
A02_0080	Engineer's confirmation of satisfactory implementation of Environmental Management Pl.	0		01-Nov-14 A		01-Nov-14			[Gantt Chart Data]												
A3 Satisfactory Implementation of Specified Plans (25-Jan'15)																					
A03_0010	Engineer's confirmation of satisfactory implementation of System Assurance Plan (25-Jan'15)	0		24-Jan-15 A		24-Jan-15			[Gantt Chart Data]												
A03_0020	Engineer's confirmation of satisfactory implementation of Health & Safety Plan (25-Jan'15)	0		24-Jan-15 A		24-Jan-15			[Gantt Chart Data]												
A03_0030	Engineer's confirmation of satisfactory implementation of Quality Plan (25-Jan'15)	0		24-Jan-15 A		24-Jan-15			[Gantt Chart Data]												
A03_0040	Engineer's confirmation of satisfactory implementation of Environmental Management Pl.	0		24-Jan-15 A		24-Jan-15			[Gantt Chart Data]												
A4 Approval of excavation method under Tram Track; Satisfactory Implementation of PMS (3-May'15)																					
A04_0010	Approval for method of excavation & support for mined tunnel section beneath tram track	0		21-Apr-15 A		07-Jul-15			[Gantt Chart Data]												
A04_0020	Engineer's confirmation of satisfactory implementation of Programming Management Sy.	0		02-May-15 A		01-Jun-15			[Gantt Chart Data]												
A5 Approval of WAC D-wall demolition; Satisfactory Implementation of Specified Plans (2-Aug'15)																					
A05_0010	Approval for method for demolition of WAC Diaphragm Wall (2-Aug'15)	0		21-Jul-15 A		23-Mar-16			[Gantt Chart Data]												
A05_0020	Engineer's confirmation of satisfactory implementation of Specified Plans (2-Aug'15)	0		30-Sep-15 A		30-Sep-15			[Gantt Chart Data]												
A6 Satisfactory Implementation of PMS (1-Nov'15)																					
A06_0010	Engineer's confirmation of satisfactory implementation of Programming Management Sy.	0		30-Sep-15 A		30-Sep-15			[Gantt Chart Data]												
A7 Satisfactory Implementation of Specified Plans (31-Jan'16)																					
A07_0010	Engineer's confirmation of satisfactory implementation of Specified Plans (31-Jan'16)	0		30-Jan-16 A		31-Mar-16			[Gantt Chart Data]												
A8 AIP for T&C of BS and ABWF works; Satisfactory Implementation of PMS (1-May'16)																					
A08_0010	Engineer's confirmation of satisfactory implementation of Programming Management Sy.	0		03-Mar-16 A		30-Apr-16			[Gantt Chart Data]												
A08_0020	Approval in principle of all procedures for Testing & Commissioning of all Building Service	0		26-Sep-17		26-Sep-17	-212	0	[Gantt Chart Data]												

- Actual Level of Effort
- Primary Baseline
- Actual Work
- Remaining Work
- Critical Remaining ...
- Baseline Milestone
- Milestone

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)											
A08_0030	Approval in principle of all acceptance procedures of all of the ABWF works (1-May'16)	0		26-Sep-17		26-Sep-17	-212	0	[Gantt Chart: Milestone diamond at 26-Sep-17]											
A9 Satisfactory Implementation of Specified Plans (31-Jul'16)																				
A09_0010	Engineer's confirmation of satisfactory implementation of System Assurance Plan (31-Jul	0		31-Oct-16		31-Oct-16	119	0	[Gantt Chart: Milestone diamond at 31-Oct-16]											
A09_0020	Engineer's confirmation of satisfactory implementation of Health & Safety Plan (31-Jul'16)	0		31-Oct-16		31-Oct-16	119	0	[Gantt Chart: Milestone diamond at 31-Oct-16]											
A09_0030	Engineer's confirmation of satisfactory implementation of Quality Plan (31-Jul'16)	0		31-Oct-16		31-Oct-16	119	0	[Gantt Chart: Milestone diamond at 31-Oct-16]											
A09_0040	Engineer's confirmation of satisfactory implementation of Environmental Management Pl	0		31-Oct-16		31-Oct-16	119	0	[Gantt Chart: Milestone diamond at 31-Oct-16]											
A10 AIP Draft O&M manual & Draft As-built Drawings; Satisfactory Implementation of PMS (30-Oct'16)																				
A10_0010	Engineer's confirmation of satisfactory implementation of Programming Management Sy	0		31-Oct-16		31-Oct-16	119	520	[Gantt Chart: Milestone diamond at 31-Oct-16]											
A10_0020	Approval in principle of draft Operating & Maintenance Manuals for the Whole Works (31	0		03-Apr-18		03-Apr-18	-401	0	[Gantt Chart: Milestone diamond at 03-Apr-18]											
A10_0030	Approval in principle of draft As-built Drawings for the Whole Works (30-Oct'16)	0		03-Apr-18		03-Apr-18	-401	0	[Gantt Chart: Milestone diamond at 03-Apr-18]											
A11 Approval of O&M manual and As-built drawings for the Works (26-Feb'17)																				
A11_0010	Approval of Operating & Maintenance Manual for Whole Works (26-Feb'17)	0		28-Jul-18		28-Jul-18	-517	0	[Gantt Chart: Milestone diamond at 28-Jul-18]											
A11_0020	Approval of As-built drawings for Whole Works (26-Feb'17)	0		28-Jul-18		28-Jul-18	-517	0	[Gantt Chart: Milestone diamond at 28-Jul-18]											
Cost Centre A: Preliminaries and General Items																				
Design, ICE, Submission and Approval																				
Design, IEC, TMLG Submission and Approval																				
D.I.T_0010	TTMS - Submission to Members of TMLG for Approval, ref. ITT 6.2	4	14-Apr-14 A	17-Apr-14 A	14-Apr-14	17-Apr-14			[Gantt Chart: Bar from 14-Apr-14 to 17-Apr-14]											
D.I.T_0020	TTMS - TMLG Meetings and Approval, Resubmission if required, RMO Applications	55	22-Apr-14 A	27-Jun-14 A	22-Apr-14	27-Jun-14			[Gantt Chart: Bar from 22-Apr-14 to 27-Jun-14]											
Design, ICE, BD Submission and Approval																				
D.I.T_0030	A1 - ELS & Temporary Decking - Design, ICE, Submission to BD for Approval	30	14-Apr-14 A	11-Aug-14 A	14-Apr-14	23-May-14			[Gantt Chart: Bar from 14-Apr-14 to 23-May-14]											
D.I.T_0040	A1 - ELS & Temporary Decking - Review the submission	30	12-Aug-14 A	16-Sep-14 A	24-May-14	28-Jun-14			[Gantt Chart: Bar from 24-May-14 to 28-Jun-14]											
D.I.T_0050	A1 - ELS & Temporary Decking - Preparation of re-submission (If Require)	14	17-Sep-14 A	23-Sep-14 A	30-Jun-14	16-Jul-14			[Gantt Chart: Bar from 30-Jun-14 to 16-Jul-14]											
D.I.T_0060	A1 - ELS & Temporary Decking - BD Review, Resubmission if required, and Approval (If	14	24-Sep-14 A	03-Mar-15 A	17-Jul-14	01-Aug-14			[Gantt Chart: Bar from 17-Jul-14 to 01-Aug-14]											
D.I.T_0070	A1 - ELS - Verification (based on 4 additional SI. AD-01 to AD-04), ICE	17	29-Jul-14 A	16-Aug-14 A	29-Jul-14	16-Aug-14			[Gantt Chart: Bar from 29-Jul-14 to 16-Aug-14]											
D.I.T_0080	A1 - ELS - Verification (based on 4 additional SI. AD-01 to AD-04), ICE, Submission & Ap	24	18-Aug-14 A	15-Sep-14 A	18-Aug-14	15-Sep-14			[Gantt Chart: Bar from 18-Aug-14 to 15-Sep-14]											
D.I.T_0090	Independent Checking Engineer - Preparation & Submission for Approval	30	14-Apr-14 A	23-May-14 A	14-Apr-14	23-May-14			[Gantt Chart: Bar from 14-Apr-14 to 23-May-14]											
D.I.T_0100	Independent Checking Engineer - Review the submission	30	24-May-14 A	28-Jun-14 A	24-May-14	28-Jun-14			[Gantt Chart: Bar from 24-May-14 to 28-Jun-14]											
D.I.T_0110	Independent Checking Engineer - Preparation of re-submission (If Require)	14	30-Jun-14 A	16-Jul-14 A	30-Jun-14	16-Jul-14			[Gantt Chart: Bar from 30-Jun-14 to 16-Jul-14]											
D.I.T_0120	Independent Checking Engineer - Resubmission if required, & Approval (If Require)	14	17-Jul-14 A	01-Aug-14 A	17-Jul-14	01-Aug-14			[Gantt Chart: Bar from 17-Jul-14 to 01-Aug-14]											
D.I.T_0130	A2 - Excavation support system for the mined tunnel section design - Prepare, ICE and	104	14-Apr-14 A	05-Dec-14 A	14-Apr-14	20-Aug-14			[Gantt Chart: Bar from 14-Apr-14 to 20-Aug-14]											
D.I.T_0140	A2 - Excavation support system for the mined tunnel section design - Review submission	24	06-Dec-14 A	23-Dec-14 A	14-Apr-14	16-May-14			[Gantt Chart: Bar from 14-Apr-14 to 16-May-14]											
D.I.T_0150	A2 - Excavation support system for the mined tunnel section design - Address comments	12	24-Dec-14 A	03-Jan-15 A	29-Jul-14	11-Aug-14			[Gantt Chart: Bar from 29-Jul-14 to 11-Aug-14]											
D.I.T_0160	A2 - Excavation support system for the mined tunnel section design - Review & Approval	24	05-Jan-15 A	01-Feb-15 A	12-Aug-14	08-Sep-14			[Gantt Chart: Bar from 12-Aug-14 to 08-Sep-14]											
D.I.T_0170	A4 - Excavation method under tram track and TW design - Prepare, ICE and submission	55	14-Apr-14 A	05-Dec-14 A	16-Jul-15	17-Sep-15			[Gantt Chart: Bar from 16-Jul-15 to 17-Sep-15]											
D.I.T_0180	A4 - Excavation method under tram track and TW design - Review submission	30	06-Dec-14 A	23-Dec-14 A	18-Sep-15	26-Oct-15			[Gantt Chart: Bar from 18-Sep-15 to 26-Oct-15]											
D.I.T_0190	A4 - Excavation method under tram track and TW design - Address comments, ICE & R	30	24-Dec-14 A	03-Jan-15 A	27-Oct-15	30-Nov-15			[Gantt Chart: Bar from 27-Oct-15 to 30-Nov-15]											
D.I.T_0200	A4 - Excavation method under tram track and TW design - Review & Approval (if require	30	05-Jan-15 A	21-Apr-15 A	01-Dec-15	07-Jan-16			[Gantt Chart: Bar from 01-Dec-15 to 07-Jan-16]											
Contractor Submission and Approval																				
Programming, Specified Plans and Hoarding Plan																				
P.S.P.H_0010	Submission schedule - Preparation & submission	30	14-Apr-14 A	14-May-14 A	31-Mar-15	09-May-15			[Gantt Chart: Bar from 31-Mar-15 to 09-May-15]											
P.S.P.H_0020	Submission schedule - Review & Approval	30	15-May-14 A	30-Jun-14 A	11-May-15	15-Jun-15			[Gantt Chart: Bar from 11-May-15 to 15-Jun-15]											
P.S.P.H_0030	Submission schedule - Preparation for Re-submission (If Require)	14	13-Jun-14 A	26-Jun-14 A	16-Jun-15	03-Jul-15			[Gantt Chart: Bar from 16-Jun-15 to 03-Jul-15]											
P.S.P.H_0040	Submission schedule - Review and Approval (If Require)	14	27-Jun-14 A	11-Jul-14 A	04-Jul-15	20-Jul-15			[Gantt Chart: Bar from 04-Jul-15 to 20-Jul-15]											
P.S.P.H_0050	Initial Three Month Rolling Program - Preparation & submission	14	14-Apr-14 A	28-Apr-14 A	31-Mar-15	20-Apr-15			[Gantt Chart: Bar from 31-Mar-15 to 20-Apr-15]											
P.S.P.H_0060	Initial Three Month Rolling Program - Review & Approval	30	29-Apr-14 A	28-May-14 A	21-Apr-15	27-May-15			[Gantt Chart: Bar from 21-Apr-15 to 27-May-15]											
P.S.P.H_0070	Initial Three Month Rolling Program - Preparation for Re-submission (If Require)	14	29-May-14 A	12-Jun-14 A	28-May-15	12-Jun-15			[Gantt Chart: Bar from 28-May-15 to 12-Jun-15]											
P.S.P.H_0080	Initial Three Month Rolling Program - Review and Approval (If Require)	14	13-Jun-14 A	26-Jun-14 A	13-Jun-15	30-Jun-15			[Gantt Chart: Bar from 13-Jun-15 to 30-Jun-15]											
P.S.P.H_0090	Preliminary Master Program - Preparation & submission	47	14-Apr-14 A	20-Jun-14 A	31-Mar-15	30-May-15			[Gantt Chart: Bar from 31-Mar-15 to 30-May-15]											
P.S.P.H_0100	Preliminary Master Program - Review & Approval	14	21-Jun-14 A	19-Jul-14 A	01-Jun-15	16-Jun-15			[Gantt Chart: Bar from 01-Jun-15 to 16-Jun-15]											

- Actual Level of Effort
- Critical Remaining ...
- Primary Baseline
- Baseline Milestone
- Actual Work
- Milestone
- Remaining Work

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)




Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)											
P.SP.H_0110	Preliminary Master Program - Preparation for Re-submission (If Require)	14	16-Sep-14 A	30-Sep-14 A	17-Jun-15	04-Jul-15			[Gantt bar from Sep-14 to Sep-14]											
P.SP.H_0120	Preliminary Master Program - Review and Approval (If Require)	14	30-Sep-14 A	22-Oct-14 A	06-Jul-15	21-Jul-15			[Gantt bar from Sep-14 to Oct-14]											
P.SP.H_0130	Specified Plans (QP, SAP, PMS, H&SP, EP) - Preparation & submission	30	14-Apr-14 A	23-May-14 A	31-Mar-15	09-May-15			[Gantt bar from Apr-14 to May-14]											
P.SP.H_0140	Specified Plans (QP, SAP, PMS, H&SP, EP) - Review & Approval	14	24-May-14 A	10-Jun-14 A	11-May-15	27-May-15			[Gantt bar from May-14 to Jun-14]											
P.SP.H_0150	Specified Plans (QP, SAP, PMS, H&SP, EP) - Preparation for Re-submission (If Require)	14	11-Jun-14 A	26-Jun-14 A	28-May-15	12-Jun-15			[Gantt bar from Jun-14 to Jun-14]											
P.SP.H_0160	Specified Plans (QP, SAP, PMS, H&SP, EP) - Review and Approval (If Require)	30	24-Jun-14 A	01-Aug-14 A	13-Jun-15	20-Jul-15			[Gantt bar from Jun-14 to Aug-14]											
P.SP.H_0170	Environmental management plan - Preparation & submission	30	14-Apr-14 A	14-May-14 A	31-Mar-15	09-May-15			[Gantt bar from Apr-14 to May-14]											
P.SP.H_0180	Environmental management plan - Review & Approval	30	15-May-14 A	12-Jun-14 A	11-May-15	15-Jun-15			[Gantt bar from May-14 to Jun-14]											
P.SP.H_0190	Environmental management plan - Preparation for Re-submission (If Require)	14	13-Jun-14 A	26-Jun-14 A	16-Jun-15	03-Jul-15			[Gantt bar from Jun-14 to Jun-14]											
P.SP.H_0200	Environmental management plan - Review and Approval (If Require)	14	27-Jun-14 A	11-Jul-14 A	04-Jul-15	20-Jul-15			[Gantt bar from Jun-14 to Jul-14]											
P.SP.H_0210	Appoint Environmental team- submit for engineer approval	30	14-Apr-14 A	23-May-14 A	31-Mar-15	09-May-15			[Gantt bar from Apr-14 to May-14]											
P.SP.H_0220	Appoint Environmental team - Review & Approval	30	27-Jun-14 A	11-Jul-14 A	11-May-15	15-Jun-15			[Gantt bar from Jun-14 to Jul-14]											
P.SP.H_0230	Appoint Environmental team - Preparation for Re-submission (If Require)	14	14-Apr-14 A	14-May-14 A	16-Jun-15	03-Jul-15			[Gantt bar from Apr-14 to May-14]											
P.SP.H_0240	Appoint Environmental team - Review and Approval (If Require)	14	27-Jun-14 A	11-Jul-14 A	04-Jul-15	20-Jul-15			[Gantt bar from Jun-14 to Jul-14]											
P.SP.H_0250	Quality Plan - Preparation & submission	30	14-Apr-14 A	14-May-14 A	31-Mar-15	09-May-15			[Gantt bar from Apr-14 to May-14]											
P.SP.H_0260	Quality Plan - Review & Approval	30	15-May-14 A	12-Jun-14 A	11-May-15	15-Jun-15			[Gantt bar from May-14 to Jun-14]											
P.SP.H_0270	Quality Plan - Preparation for Re-submission (If Require)	14	13-Jun-14 A	26-Jun-14 A	16-Jun-15	03-Jul-15			[Gantt bar from Jun-14 to Jun-14]											
P.SP.H_0280	Quality Plan - Review and Approval (If Require)	14	17-Jun-14 A	11-Jul-14 A	04-Jul-15	20-Jul-15			[Gantt bar from Jun-14 to Jul-14]											
P.SP.H_0290	Health and Safety Plan - Preparation & submission	30	14-Apr-14 A	14-May-14 A	31-Mar-15	09-May-15			[Gantt bar from Apr-14 to May-14]											
P.SP.H_0300	Health and Safety Plan - Review & Approval	30	15-May-14 A	12-Jun-14 A	11-May-15	15-Jun-15			[Gantt bar from May-14 to Jun-14]											
P.SP.H_0310	Health and Safety Plan - Preparation for Re-submission (If Require)	14	13-Jun-14 A	26-Jun-14 A	16-Jun-15	03-Jul-15			[Gantt bar from Jun-14 to Jun-14]											
P.SP.H_0320	Health and Safety Plan - Review and Approval (If Require)	14	27-Jun-14 A	11-Jul-14 A	04-Jul-15	20-Jul-15			[Gantt bar from Jun-14 to Jul-14]											
P.SP.H_0330	System Assurance Plan - Preparation & submission	30	14-Apr-14 A	14-May-14 A	31-Mar-15	09-May-15			[Gantt bar from Apr-14 to May-14]											
P.SP.H_0340	System Assurance Plan - Review & Approval	30	15-May-14 A	12-Jun-14 A	11-May-15	15-Jun-15			[Gantt bar from May-14 to Jun-14]											
P.SP.H_0350	System Assurance Plan - Preparation for Re-submission (If Require)	14	13-Jun-14 A	26-Jun-14 A	16-Jun-15	03-Jul-15			[Gantt bar from Jun-14 to Jun-14]											
P.SP.H_0360	System Assurance Plan - Review and Approval (If Require)	14	27-Jun-14 A	11-Jul-14 A	04-Jul-15	20-Jul-15			[Gantt bar from Jun-14 to Jul-14]											
P.SP.H_0370	A2 Hoarding phase - Preparation & submission	100	14-Apr-14 A	30-Apr-14 A	31-Mar-15	03-Aug-15			[Gantt bar from Apr-14 to Apr-14]											
P.SP.H_0380	A2 Hoarding phase - Review & Approval	24	02-May-14 A	30-May-14 A	04-Aug-15	31-Aug-15			[Gantt bar from May-14 to May-14]											
P.SP.H_0390	A2 Hoarding phase - Preparation for Re-submission (If Require)	12	31-May-14 A	14-Jun-14 A	01-Sep-15	14-Sep-15			[Gantt bar from May-14 to Jun-14]											
P.SP.H_0400	A2 Hoarding phase - Review and Approval (If Require)	24	16-Jun-14 A	28-Jun-14 A	15-Sep-15	14-Oct-15			[Gantt bar from Jun-14 to Jun-14]											
Implementation of Specified Plans																				
SPA02_0010	A2 Satisfactory Implementation of Quality Plan	0		01-Nov-14 A		20-Jul-15			[Milestone diamond at Nov-14]											
SPA03_0010	A3 Satisfactory Implementation of System Assurance Plan	0		01-Nov-14 A		20-Jul-15			[Milestone diamond at Nov-14]											
SPA03_0020	A3 Satisfactory Implementation of Health and Safety Plan	0		01-Nov-14 A		20-Jul-15			[Milestone diamond at Nov-14]											
SPA03_0030	A3 Satisfactory Implementation of Environmental Management Plan	0		01-Nov-14 A		20-Jul-15			[Milestone diamond at Nov-14]											
SPA03_0040	A3 Satisfactory Implementation of Quality Plan	0		24-Jan-15 A		20-Jul-15			[Milestone diamond at Jan-15]											
SPA03_0050	A3 Satisfactory Implementation of System Assurance Plan	0		24-Jan-15 A		20-Jul-15			[Milestone diamond at Jan-15]											
SPA03_0060	A3 Satisfactory Implementation of Health and Safety Plan	0		24-Jan-15 A		20-Jul-15			[Milestone diamond at Jan-15]											
SPA03_0070	A3 Satisfactory Implementation of Environmental Management Plan	0		24-Jan-15 A		20-Jul-15			[Milestone diamond at Jan-15]											
SPA05_0010	A5 Satisfactory Implementation of Quality Plan	0		01-Aug-15 A		01-Aug-15			[Milestone diamond at Aug-15]											
SPA05_0020	A5 Satisfactory Implementation of System Assurance Plan	0		01-Aug-15 A		01-Aug-15			[Milestone diamond at Aug-15]											
SPA05_0030	A5 Satisfactory Implementation of Health and Safety Plan	0		01-Aug-15 A		01-Aug-15			[Milestone diamond at Aug-15]											
SPA05_0040	A5 Satisfactory Implementation of Environmental Management Plan	0		01-Aug-15 A		01-Aug-15			[Milestone diamond at Aug-15]											
SPA07_0010	A7 Satisfactory Implementation of Quality Plan	0		30-Jan-16 A		29-Feb-16			[Milestone diamond at Jan-16]											
SPA07_0020	A7 Satisfactory Implementation of System Assurance Plan	0		30-Jan-16 A		29-Feb-16			[Milestone diamond at Jan-16]											
SPA07_0030	A7 Satisfactory Implementation of Health and Safety Plan	0		30-Jan-16 A		29-Feb-16			[Milestone diamond at Jan-16]											
SPA07_0040	A7 Satisfactory Implementation of Environmental Management Plan	0		30-Jan-16 A		29-Feb-16			[Milestone diamond at Jan-16]											
SPA09_0010	A9 Satisfactory Implementation of Quality Plan	0		31-Oct-16*		31-Oct-16	-92	0	[Milestone diamond at Oct-16]											
SPA09_0020	A9 Satisfactory Implementation of System Assurance Plan	0		31-Oct-16*		31-Oct-16	-92	0	[Milestone diamond at Oct-16]											

■ Actual Level of Effort ■ Critical Remaining ...
■ Primary Baseline ◆ Baseline Milestone
■ Actual Work ◆ Milestone
■ Remaining Work

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)											
SPA09_0030	A9 Satisfactory Implementation of Health and Safety Plan	0		31-Oct-16*		31-Oct-16	-92	0	[Gantt bar for SPA09_0030]											
SPA09_0040	A9 Satisfactory Implementation of Environmental Management Plan	0		31-Oct-16*		31-Oct-16	-92	0	[Gantt bar for SPA09_0040]											
Implementation of Programming Management System																				
PMS.A02_0010	A2 Satisfactory Implementation of Programming Management System	0	01-Nov-14 A			21-Jul-15			[Gantt bar for PMS.A02_0010]											
PMS.A04_0010	A4 Satisfactory Implementation of Programming Management System	0	02-May-15 A			01-Jun-15			[Gantt bar for PMS.A04_0010]											
PMS.A06_0010	A6 Satisfactory Implementation of Programming Management System	0	28-Aug-15 A			31-Oct-15			[Gantt bar for PMS.A06_0010]											
PMS.A08_0010	A8 Satisfactory Implementation of Programming Management System	0	03-Mar-16 A			30-Apr-16			[Gantt bar for PMS.A08_0010]											
PMS.A10_0010	A10 Satisfactory Implementation of Programming Management System	0	31-Oct-16*			31-Oct-16	-1	0	[Gantt bar for PMS.A10_0010]											
Other Submissions and O&M Manual																				
OS.OM_0010	Hoarding Installation Method Statement - Preparation & Submission	30	14-Apr-14 A	23-May-14 A	31-Mar-15	09-May-15			[Gantt bar for OS.OM_0010]											
OS.OM_0020	Hoarding Installation Method Statement - Review & Approval	12	24-May-14 A	07-Jun-14 A	11-May-15	23-May-15			[Gantt bar for OS.OM_0020]											
OS.OM_0030	Hoarding Installation Method Statement - Preparation for Re-submission (if required)	12	09-Jun-14 A	21-Jun-14 A	26-May-15	08-Jun-15			[Gantt bar for OS.OM_0030]											
OS.OM_0040	Hoarding Installation Method Statement - Re-submission (if required) & Approval	12	23-Jun-14 A	23-Jun-14 A	09-Jun-15	23-Jun-15			[Gantt bar for OS.OM_0040]											
OS.OM_0050	Site Investigation Works Method Statement - Preparation & Submission	30	14-Apr-14 A	23-May-14 A	31-Mar-15	09-May-15			[Gantt bar for OS.OM_0050]											
OS.OM_0060	Site Investigation Works Method Statement - Review & Approval	12	24-May-14 A	07-Jun-14 A	11-May-15	23-May-15			[Gantt bar for OS.OM_0060]											
OS.OM_0070	Site Investigation Works Method Statement - Preparation for Re-submission (if required)	12	09-Jun-14 A	21-Jun-14 A	26-May-15	08-Jun-15			[Gantt bar for OS.OM_0070]											
OS.OM_0080	Site Investigation Works Method Statement - Re-submission (if required) & Approval	12	23-Jun-14 A	07-Jul-14 A	09-Jun-15	23-Jun-15			[Gantt bar for OS.OM_0080]											
OS.OM_0090	WAC D-wall demolition Design- ICE, Preparation for design submission	90	03-Nov-14 A	18-Feb-15 A	31-Jul-15	16-Nov-15			[Gantt bar for OS.OM_0090]											
OS.OM_0100	WAC D-wall demolition- Review & Approval	60	23-Feb-15 A	08-May-15 A	17-Nov-15	28-Jan-16			[Gantt bar for OS.OM_0100]											
OS.OM_0110	WAC D-wall demolition- Preparation for re-submission (If require)	40	09-May-15 A	26-Jun-15 A	29-Jan-16	18-Mar-16			[Gantt bar for OS.OM_0110]											
OS.OM_0120	WAC D-wall demolition- Review & Approval (If require)	30	27-Jun-15 A	01-Aug-15 A	19-Mar-16	27-Apr-16			[Gantt bar for OS.OM_0120]											
OS.OM_0121	H15 D-wall demolition Design- ICE, Preparation for design submission	24	30-Sep-16 A	29-Oct-16 A	30-Sep-16	29-Oct-16			[Gantt bar for OS.OM_0121]											
OS.OM_0122	H15 D-wall demolition- Review & Approval	24	31-Oct-16 A	26-Nov-16 A	31-Oct-16	26-Nov-16			[Gantt bar for OS.OM_0122]											
OS.OM_0123	H15 D-wall demolition- Preparation for re-submission (If require)	12	28-Nov-16 A	10-Dec-16 A	28-Nov-16	10-Dec-16			[Gantt bar for OS.OM_0123]											
OS.OM_0124	H15 D-wall demolition- Review & Approval (If require)	12	12-Dec-16 A	24-Dec-16 A	12-Dec-16	24-Dec-16			[Gantt bar for OS.OM_0124]											
OS.OM_0130	A8 AIP procedures for T&C of BS and ABWF works (1st Batch)	90	31-Oct-16	18-Feb-17	31-Oct-16	18-Feb-17	-419	0	[Gantt bar for OS.OM_0130]											
OS.OM_0140	A8 AIP procedures for T&C of BS and ABWF works (2nd Batch)	90	20-Feb-17	12-Jun-17	20-Feb-17	12-Jun-17	-419	0	[Gantt bar for OS.OM_0140]											
OS.OM_0150	A8 AIP procedures for T&C of BS and ABWF works (Remaining)	90	13-Jun-17	26-Sep-17	13-Jun-17	26-Sep-17	-419	0	[Gantt bar for OS.OM_0150]											
OS.OM_0160	A10 AIP of Draft O&M manual and Draft As-built Drawings	150	27-Sep-17	03-Apr-18	27-Sep-17	03-Apr-18	-419	0	[Gantt bar for OS.OM_0160]											
OS.OM_0170	A11 Approval of O&M manual and As-built drawings for the Works	95	04-Apr-18	28-Jul-18	04-Apr-18	28-Jul-18	-419	0	[Gantt bar for OS.OM_0170]											
OS.OM_0180	RC Works- Preparation of Method Statement- Preparation	60	06-Jan-15 A	06-Feb-15 A	31-Mar-15	15-Jun-15			[Gantt bar for OS.OM_0180]											
OS.OM_0190	RC Works - Preparation of Method Statement- Submission & Approval	12	06-Feb-15 A	10-Feb-15 A	03-Sep-15	16-Sep-15			[Gantt bar for OS.OM_0190]											
OS.OM_0200	RC Works - Preparation for Re-submission (if required)	12	10-Feb-15 A	16-Feb-15 A	17-Sep-15	02-Oct-15			[Gantt bar for OS.OM_0200]											
OS.OM_0210	RC Works - Re-submission (if required) & Approval	12	16-Feb-15 A	16-Feb-15 A	02-Jul-15	15-Jul-15			[Gantt bar for OS.OM_0210]											
OS.OM_0220	Sheet pile installation- Preparation of Method Statement- Preparation	42	03-Jun-14 A	03-Jul-14 A	31-Mar-15	23-May-15			[Gantt bar for OS.OM_0220]											
OS.OM_0230	Sheet pile installation- Preparation of Method Statement- Submission & Approval	12	03-Jul-14 A	08-Jul-14 A	26-May-15	08-Jun-15			[Gantt bar for OS.OM_0230]											
OS.OM_0240	Sheet pile installation - Preparation for Re-submission (if required)	12	08-Jul-14 A	23-Oct-14 A	09-Jun-15	23-Jun-15			[Gantt bar for OS.OM_0240]											
OS.OM_0250	Sheet pile installation - Re-submission (if required) & Approval	12	23-Oct-14 A	14-Nov-14 A	24-Jun-15	08-Jul-15			[Gantt bar for OS.OM_0250]											
OS.OM_0260	Excavation works- Preparation of Method Statement- Preparation	42	22-Aug-14 A	22-Sep-14 A	31-Mar-15	23-May-15			[Gantt bar for OS.OM_0260]											
OS.OM_0270	Excavation works- Preparation of Method Statement- Submission & Approval	12	22-Sep-14 A	21-Oct-14 A	26-May-15	08-Jun-15			[Gantt bar for OS.OM_0270]											
OS.OM_0280	Excavation works- Preparation for Re-submission (if required)	12	21-Oct-14 A	21-Oct-14 A	09-Jun-15	23-Jun-15			[Gantt bar for OS.OM_0280]											
OS.OM_0290	Excavation works- Re-submission (if required) & Approval	12	21-Oct-14 A	21-Oct-14 A	24-Jun-15	08-Jul-15			[Gantt bar for OS.OM_0290]											
OS.OM_0300	Work below tram track Method Statement - Preparation	60	23-Feb-15 A	23-Mar-15 A	24-Jun-15	02-Sep-15			[Gantt bar for OS.OM_0300]											
OS.OM_0310	Work below tram track Method Statement - Submission & Approval	12	23-Mar-15 A	09-Apr-15 A	03-Sep-15	16-Sep-15			[Gantt bar for OS.OM_0310]											
OS.OM_0320	Work below tram track Method Statement - Preparation for Re-submission (if required)	12	09-Apr-15 A	27-Apr-15 A	11-Apr-15	24-Apr-15			[Gantt bar for OS.OM_0320]											
OS.OM_0330	Work below tram track Method Statement - Re-submission (if required) & Approval	12	27-Apr-15 A	10-Jun-15 A	30-Jun-15	14-Jul-15			[Gantt bar for OS.OM_0330]											
OS.OM_0340	H15 & WAC Break Through Method Statement - Preparation	48	11-Jun-15 A	20-Jul-15 A	30-Jun-15	25-Aug-15			[Gantt bar for OS.OM_0340]											
OS.OM_0350	H15 & WAC Break Through Method Statement - Submission & Approval	12	20-Jul-15 A	21-Jul-15 A	05-Aug-15	18-Aug-15			[Gantt bar for OS.OM_0350]											
OS.OM_0360	H15 & WAC Break Through Method Statement - Preparation for Re-submission (if requ	12	21-Jul-15 A	21-Jul-15 A	19-Aug-15	01-Sep-15			[Gantt bar for OS.OM_0360]											

- █ Actual Level of Effort
- █ Primary Baseline
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining ...
- ◆ Baseline Milestone
- ◆ Milestone

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)												
OS.OM_0370	H15 & WAC Break Through Method Statement - Re-submission (if required) & Approva	12	21-Jul-15 A	21-Jul-15 A	02-Sep-15	15-Sep-15			[Gantt bars for OS.OM_0370]												
OS.OM_0380	BD for consent of H15 break throughs works - Preparation	24	03-Aug-15 A	12-Nov-16	24-Sep-16	24-Oct-16	-189	0	[Gantt bars for OS.OM_0380]												
OS.OM_0390	BD for consent of H15 break throughs works - Submission & Approval	24	14-Nov-16	10-Dec-16	14-Nov-16	10-Dec-16	-189	0	[Gantt bars for OS.OM_0390]												
OS.OM_0400	BD for consent of H15 break throughs works - Preparation for Re-submission (if require	12	12-Dec-16	24-Dec-16	12-Dec-16	24-Dec-16	-189	0	[Gantt bars for OS.OM_0400]												
OS.OM_0410	BD for consent of H15 break throughs works - Re-submission (if required) & Approval	12	28-Dec-16	11-Jan-17	28-Dec-16	11-Jan-17	-189	71	[Gantt bars for OS.OM_0410]												
OS.OM_0420	Submit and obtain AIP for Method Statement, EDOC Draft, Permanent Materials	60	31-Jul-15 A	10-Oct-15 A	31-Jul-15	10-Oct-15			[Gantt bars for OS.OM_0420]												
Mobilization and Other Preliminaries																					
Permit Applications																					
PA_0010	XP Excavation Permit Application and Permit	70	14-Apr-14 A	10-Jun-14 A	31-Mar-15	27-Jun-15			[Gantt bars for PA_0010]												
PA_0020	TRA Tree Removal Application and Permit	6	14-Apr-14 A	15-Jul-14 A	31-Mar-15	10-Apr-15			[Gantt bars for PA_0020]												
PA_0030	Liason with all utility service providers on diversions	42	14-Apr-14 A	11-Jul-14 A	31-Mar-15	23-May-15			[Gantt bars for PA_0030]												
PA_0040	Baseline noise monitoring report - Preparation & submission to Engineer and EPD	30	23-Jun-14 A	28-Jun-14 A	31-Mar-15	09-May-15			[Gantt bars for PA_0040]												
PA_0050	Baseline noise monitoring report - Review & Approval	30	30-Jun-14 A	09-Jul-14 A	11-May-15	15-Jun-15			[Gantt bars for PA_0050]												
PA_0060	Baseline noise monitoring report - Preparation for Re-submission (If Require)	14	23-Jun-14 A	28-Jun-14 A	16-Jun-15	03-Jul-15			[Gantt bars for PA_0060]												
PA_0070	Baseline noise monitoring report - Review and Approval (If Require)	14	30-Jun-14 A	09-Jul-14 A	04-Jul-15	20-Jul-15			[Gantt bars for PA_0070]												
PA_0080	Baseline air monitoring report - Preparation & submission to Engineer and EPD	30	23-Jun-14 A	28-Jun-14 A	31-Mar-15	09-May-15			[Gantt bars for PA_0080]												
PA_0090	Baseline air monitoring report - Review & Approval	30	30-Jun-14 A	09-Jul-14 A	11-May-15	15-Jun-15			[Gantt bars for PA_0090]												
PA_0100	Baseline air monitoring report - Preparation for Re-submission (If Require)	14	10-Jul-14 A	10-Jul-14 A	16-Jun-15	03-Jul-15			[Gantt bars for PA_0100]												
PA_0110	Baseline air monitoring report - Review and Approval (If Require)	14	10-Jun-14 A	11-Jul-14 A	04-Jul-15	20-Jul-15			[Gantt bars for PA_0110]												
B : Civil, Structural and ABWF Works for the New Subway (Part A Works)																					
Cost Centre B - Milestone Schedules																					
B1 Excavate to +2.5 of SBC & Children's Play Area Cofferdam completed (2-Nov'14)																					
MSB01_01	Southern Basket Ball Court: excavate to +2.5mPD (2-Nov'14)	0		01-Nov-14 A		19-Oct-15			[Milestone diamond]												
MSB01_02	Children's Play Area - Cofferdam construction is completed (2-Nov'14)	0		25-Oct-14 A		10-Jul-15			[Milestone diamond]												
B2 SBC Excavation complete & Children's Play Area Excavation to -1.3mPD (25-Jan'15)																					
MSB02_01	Southern Basket Ball Court: Excavation is satisfactorily completed (25-Jan'15)	0		16-Jan-15 A		12-Jan-16			[Milestone diamond]												
MSB02_02	Children's Play Area: Excavation has reached -1.3mPD (25-Jan'15)	0		24-Jan-15 A		12-Jan-16			[Milestone diamond]												
B3 SBC RC Roof, JnR NFP & EBC 67% cofferdam, JnR WBC UU div complete (3-May'15)																					
MSB03_01	Southern Basket Ball Court: Roof slab construction has been satisfactorily completed (3-	0		28-Apr-15 A		31-Mar-15			[Milestone diamond]												
MSB03_02	Johnston Road North Footpath and East-bound Carriageway: 67% of cofferdam installa	0		09-May-15 A		23-May-15			[Milestone diamond]												
MSB03_03	Johnston Road West-bound Carriageway - All utility diversions, where required, satisfact	0		21-Mar-15 A		30-Jun-15			[Milestone diamond]												
MSB03_04	10% completed of tram track support (3-May'15)	0		29-Apr-15 A		29-May-15			[Milestone diamond]												
B4 SBC return, NBC Site entry, CPA base, JnR NFP & EBC Cofferdam & decks complete (2-Aug'15)																					
MSB04_01	Southern Basket Ball Court: Playing surface has been returned to LCSD for use (2-Aug'	0		11-Aug-15 A		01-Aug-15			[Milestone diamond]												
MSB04_02	Northern Basket Ball Court: Site entry onto Hennessy Road has been formed (2-Aug'15	0		15-Aug-15 A		30-Sep-15			[Milestone diamond]												
MSB04_03	Children's Play Area: RC construction of the base slab, except at mucking out point, com	0		17-Jul-15 A		30-Sep-15			[Milestone diamond]												
MSB04_04	JnR N-Footpath & E-Bound Carriageway: Cofferdam construction complete & all temp t	0		31-Oct-16		31-Oct-16	119	0	[Milestone diamond]												
B5 NBC cofferdam, CPA RC & vent shaft 1.2m above GL, Tram Tracks Excavation to +0.0mPD (1-Nov'15)																					
MSB05_01	Northern Basket Ball Court: Satisfactorily complete construction of the cofferdam (1-Nov	0		18-Dec-16 A		29-Feb-16			[Milestone diamond]												
MSB05_02	Children's Play Area: RC construction complete include above ground vent shaft structur	0		09-Nov-16		09-Nov-16	109	0	[Milestone diamond]												
MSB05_03	Tram Tracks - Excavation to +0.0 mPD is satisfactorily completed (1-Nov'15)	0		31-Oct-16		31-Oct-16	119	10	[Milestone diamond]												
B6 NBC Excavation to formation, JnR Excavation complete (31-Jan'16)																					
MSB06_01	Northern basket Ball Court - Excavation to final formation has been satisfactorily complet	0		28-Dec-15 A		31-Mar-16			[Milestone diamond]												
MSB06_02	Johnston Road All Carriageways, Footpaths & Tram Tracks: Excavation is completed (3'	0		07-Jan-17		07-Jan-17	50	0	[Milestone diamond]												
B7 NBC RC roof, JnR CW & FP & TT RC construction exp temp opening, CPA RC complete (1-May'16)																					
MSB07_01	Northern Basket Ball Court: RC construction of the roof slab has been completed (1-Ma	0		01-Apr-16 A		25-May-16			[Milestone diamond]												
MSB07_02	JnR Carriageways, Footpaths & Tram Tracks: RC construction, except at temporary ope	0		05-Apr-17		05-Apr-17	-38	0	[Milestone diamond]												
MSB07_03	Children's Play Area: RC Construction of above ground ventilation shaft structures is con	0		14-Dec-16		14-Dec-16	74	112	[Milestone diamond]												
B8 ABWF Degree1 achieved, NBC All reinstatement, Opening through H15 D-wall complete (31-Jul'16)																					

- Actual Level of Effort
- Primary Baseline
- Actual Work
- Remaining Work
- Critical Remaining ...
- Baseline Milestone
- Milestone

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart														
									2014	2015			2016			2017			2018				
MSB08_01	ABWF to Degree 1 has been achieved for works in this cost centre (31-Jul'16)	0		06-Jul-17		06-Jul-17	-130	0															
MSB08_02	Northern Basket Ball Court - All re-surfacing works & playing surface reinstatement complete	0		23-Dec-16		23-Dec-16	66	196															
MSB08_03	H15 Interface: The opening through H15 diaphragm wall has been formed (31-Jul'16)	0		30-Jun-17		30-Jun-17	-124	6															
B9 ABWF Degree3 achieved, All road reinstatement in JnR & Hennessy Rd complete (30-Oct'16)																							
MSB09_01	ABWF to Degree 3 has been achieved for works in this cost centre (30-Oct'16)	0		07-Sep-17		07-Sep-17	-192	0															
MSB09_02	All road reinstatement works in Johnston Road and Hennessy Road have been satisfactorily completed	0		21-Jun-17		21-Jun-17	-115	77															
B10 All works in Cost Centre B satisfactorily completed (26-Feb'17)																							
MSB10_01	All works in this cost centre have been satisfactorily completed (26-Feb'17)	0		17-Oct-17		17-Oct-17	-233	70															
Degrees of completion for ABWF Works																							
ABWF.D1	ABWF Works - Degree 1	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D2	ABWF Works - Degree 2	0		07-Aug-17		07-Aug-17	-161	31															
ABWF.D3	ABWF Works - Degree 3	0		07-Sep-17		07-Sep-17	-192	0															
ABWF Works - Degree 1																							
ABWF.D1_1.010	1.1- Structure and building complete, clean, dry and weather proof	0		23-May-17		23-May-17	-86	44															
ABWF.D1_1.020	1.2- Blockwalls and partition walls complete, except on plant access route	0		10-Jun-17		10-Jun-17	-103	27															
ABWF.D1_1.030	1.3- Plastering, undercoat painting, floor screeding including plinths & upstands complete	0		10-Jun-17		10-Jun-17	-103	27															
ABWF.D1_1.040	1.4- Equipment delivery routes & access openings available for Designated Contractors	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D1_1.050	1.5- Cast-in items & subframe installed; niches, recesses and box outs formed; cable trays installed	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D1_1.060	1.6- Structure as-built survey accepted	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D1_1.070	1.7- Structural & blockwork E&M openings formed & survey complete	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D1_1.080	1.8- Movement joints & stitch strips complete	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D1_1.090	1.9- Drainage system & discharge connections complete with temporary pumps operational	0		26-Jun-17		26-Jun-17	-120	10															
ABWF.D1_1.100	1.10- Escalator zones & pits complete; survey reference lines accepted	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D1_1.110	1.11- Earthing mat, earthing rods & earthing pits complete & test results accepted	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D1_1.120	1.12- Underground pipework complete including manholes, ductworks & drawpits	0		06-Jul-17		06-Jul-17	-130	0															
ABWF.D1_1.130	1.13- Civil & building provisions for designated & interfacing contractors complete	0		31-Oct-16		31-Oct-16	119	249															
ABWF Works - Degree 2																							
ABWF.D2_2.010	2.1- Permanent door frames installed with temporary doors and locks	0		31-Jul-17		31-Jul-17	-154	7															
ABWF.D2_2.020	2.2- Floor finishes & wall tiling in plant rooms for Designated Contractors complete	0		07-Aug-17		07-Aug-17	-161	0															
ABWF.D2_2.030	2.3- Glazing & Balustrade support installed	0		24-Jun-17		24-Jun-17	-117	44															
ABWF.D2_2.040	2.4- Metal staircases, cat-ladders & catwalks complete	0		31-Jul-17		31-Jul-17	-154	7															
ABWF.D2_2.050	2.5- External louvers installed	0		31-Jul-17		31-Jul-17	-154	7															
ABWF.D2_2.060	2.6- Framework for final finishes installed	0		31-Jul-17		31-Jul-17	-154	7															
ABWF.D2_2.070	2.7- Water tightness testing to water tanks passed	0		13-Jul-17		13-Jul-17	-137	24															
ABWF Works - Degree 3																							
ABWF.D3_3.010	3.1- All finishes complete including permanent doors, ironmongery	0		07-Sep-17		07-Sep-17	-192	0															
ABWF.D3_3.020	3.2- Balustrade installed	0		07-Sep-17		07-Sep-17	-192	0															
ABWF.D3_3.030	3.3- Signage hangers & supports installed	0		04-Sep-17		04-Sep-17	-189	3															
ABWF.D3_3.040	3.4- Roller shutters, fire shutters & smoke barriers installed	0		04-Sep-17		04-Sep-17	-189	3															
ABWF.D3_3.050	3.5- Acoustic treatment applied	0		04-Sep-17		04-Sep-17	-189	3															
ABWF.D3_3.060	3.6- Louvres & grilles installed	0		04-Sep-17		04-Sep-17	-189	3															
ABWF.D3_3.070	3.7- All openings & Penetrations sealed	0		17-Aug-17		17-Aug-17	-172	20															
Southern Playground Repronvision works																							
RW_0010	LCSD handover Northern Basket Ball Court 1	1	12-Aug-17	12-Aug-17	12-Aug-17	12-Aug-17	-190	0															
RW_0020	Fence off the site	2	14-Aug-17	15-Aug-17	14-Aug-17	15-Aug-17	-190	0															
RW_0030	Expose the surface	6	16-Aug-17	22-Aug-17	16-Aug-17	22-Aug-17	-190	0															
RW_0040	Resurfacing works	14	23-Aug-17	07-Sep-17	23-Aug-17	07-Sep-17	-190	0															
RW_0050	Hand over to LCSD, additional remedial if require	5	08-Sep-17	13-Sep-17	08-Sep-17	13-Sep-17	-190	0															
RW_0060	LCSD handover Southern Basket Ball Court 2	1	14-Sep-17	14-Sep-17	14-Sep-17	14-Sep-17	-190	0															

- Actual Level of Effort
- Primary Baseline
- Actual Work
- Remaining Work
- Critical Remaining ...
- Baseline Milestone
- Milestone

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
 Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)												
RW_0070	Fence off the site	2	15-Sep-17	16-Sep-17	15-Sep-17	16-Sep-17	-190	0	[Gantt bar for RW_0070]												
RW_0080	Expose the surface	6	18-Sep-17	23-Sep-17	18-Sep-17	23-Sep-17	-190	0	[Gantt bar for RW_0080]												
RW_0090	Resurfacing works	13	25-Sep-17	11-Oct-17	25-Sep-17	11-Oct-17	-190	0	[Gantt bar for RW_0090]												
RW_0100	Hand over to LCSD, additional remedial if require	5	12-Oct-17	17-Oct-17	12-Oct-17	17-Oct-17	-190	0	[Gantt bar for RW_0100]												
Cost Centre B: Part A Works, Civil and Structural Works for the New Subway																					
B.RC_Comp	RC Structure completed for the new subway	0		05-Apr-17		05-Apr-17	-317	0	[Gantt bar for B.RC_Comp]												
Site Preliminary Works																					
SPW_0010	LCSD handover SBC & Play's Area	3	14-Apr-14 A	16-Apr-14 A	31-Mar-15	02-Apr-15			[Gantt bar for SPW_0010]												
SPW_0020	Fence off the Site area for SBC & Play's Area	3	17-Apr-14 A	23-Apr-14 A	08-Apr-15	10-Apr-15			[Gantt bar for SPW_0020]												
SPW_0030	Employ security guard & security booth delivery	3	24-Apr-14 A	26-Apr-14 A	11-Apr-15	14-Apr-15			[Gantt bar for SPW_0030]												
SPW_0040	Removal of existing furniture for SBC & Play's Area as require	6	28-Apr-14 A	05-May-14 A	15-Apr-15	21-Apr-15			[Gantt bar for SPW_0040]												
SPW_0050	Trial trenches and expose existing UU service in SBC & Play's area	40	14-Apr-14 A	05-Jun-14 A	31-Mar-15	21-May-15			[Gantt bar for SPW_0050]												
SPW_0060	Setting up site office & misc.	50	07-May-14 A	05-Jul-14 A	22-Apr-15	22-Jun-15			[Gantt bar for SPW_0060]												
SPW_0070	Form site access for vehicle	12	07-Jul-14 A	19-Jul-14 A	23-Jun-15	07-Jul-15			[Gantt bar for SPW_0070]												
SPW_0080	Diversion of existing utilities & misc. works if require for SBC & Play's Area	24	09-Jun-14 A	07-Jul-14 A	26-May-15	23-Jun-15			[Gantt bar for SPW_0080]												
SPW_0090	Erect hoarding for SBC	12	16-Jul-14 A	29-Jul-14 A	24-Jun-15	08-Jul-15			[Gantt bar for SPW_0090]												
SPW_0100	Ground/ Site Investigation in SBC & Play's Area	18	08-Jul-14 A	28-Jul-14 A	24-Jun-15	15-Jul-15			[Gantt bar for SPW_0100]												
SPW_0110	Transplant and tree removal	72	24-Apr-14 A	21-Jul-14 A	11-Apr-15	08-Jul-15			[Gantt bar for SPW_0110]												
Northern Basket Ball Court																					
NBC_0010	Liaison with relevance parties for TTM	80	02-Apr-15 A	02-Jul-15 A	30-Jun-15	03-Oct-15			[Gantt bar for NBC_0010]												
NBC_0020	LCSD handover Northern Basket Ball Court for LTS construction works	6	11-Aug-15 A	11-Aug-15 A	01-Aug-15	08-Aug-15			[Gantt bar for NBC_0020]												
NBC_0030	Preparation works for NBC site access	4	11-Aug-15 A	11-Aug-15 A	08-Aug-15	13-Aug-15			[Gantt bar for NBC_0030]												
NBC_0040	Implementation of TTM	3	11-Aug-15 A	11-Aug-15 A	08-Aug-15	12-Aug-15			[Gantt bar for NBC_0040]												
NBC_0050	Relocation of metal fence access door for public	6	11-Aug-15 A	11-Aug-15 A	13-Aug-15	20-Aug-15			[Gantt bar for NBC_0050]												
NBC_0060	Hoarding installation, installation of site entry on Hennessy Road	5	11-Aug-15 A	15-Aug-15 A	11-Aug-15	15-Aug-15			[Gantt bar for NBC_0060]												
NBC_0070	Expose UU & trial trench for sheet piles works	12	17-Aug-15 A	20-Aug-15 A	14-Sep-15	26-Sep-15			[Gantt bar for NBC_0070]												
NBC_0080	Phase 3 ELS- Sheet Piles Installation [104 no. x 24m]	48	24-Aug-15 A	23-Sep-15 A	29-Sep-15	25-Nov-15			[Gantt bar for NBC_0080]												
NBC_0090	Curtain Grouting and remedial works for sheet piles not reaching to design toe level	15	30-Sep-15 A	13-Oct-15 A	30-Sep-15	17-Oct-15			[Gantt bar for NBC_0090]												
NBC_0100	Phase 3 ELS- Pumping Test preparation works	12	09-Oct-15 A	26-Oct-15 A	30-Sep-15	14-Oct-15			[Gantt bar for NBC_0100]												
NBC_0110	Phase 3 ELS- Pumping Test	6	27-Oct-15 A	01-Nov-15 A	19-Oct-15	26-Oct-15			[Gantt bar for NBC_0110]												
NBC_0120	Phase 3 ELS- Pumping Test Report Preparation and submission to BD	6	02-Nov-15 A	02-Nov-15 A	27-Oct-15	02-Nov-15			[Gantt bar for NBC_0120]												
NBC_0130	Bulk Excavation (Removal of hard paving on ground surface) & excavation for layer 1 to	9	04-Nov-15 A	10-Nov-15 A	03-Nov-15	12-Nov-15			[Gantt bar for NBC_0130]												
NBC_0140	Bulk excavation & layer 2 strut & preloading [500m^3]	15	11-Nov-15 A	21-Nov-15 A	13-Nov-15	30-Nov-15			[Gantt bar for NBC_0140]												
NBC_0150	Bulk excavation & layer 3 strut & preloading [500m^3]	18	23-Nov-15 A	03-Dec-15 A	08-Dec-15	31-Dec-15			[Gantt bar for NBC_0150]												
NBC_0160	Bulk excavation & layer 4 strut & preloading [500m^3]	21	04-Dec-15 A	04-Jan-16 A	31-Dec-15	26-Jan-16			[Gantt bar for NBC_0160]												
NBC_0170	Plate load test	6	05-Jan-16 A	08-Jan-16 A	20-Feb-16	27-Feb-16			[Gantt bar for NBC_0170]												
NBC_0180	Plate load test- Preparation of report & submission to BD	6	09-Jan-16 A	31-Jan-16 A	27-Feb-16	05-Mar-16			[Gantt bar for NBC_0180]												
NBC_0190	Base Slab- Waterproofing & RC construction [Concrete 490m^3] & [Re-Bar 29.5 T]	15	13-Jan-16 A	22-Jan-16 A	05-Mar-16	23-Mar-16			[Gantt bar for NBC_0190]												
NBC_0200	Wall- Waterproofing & RC construction [Concrete 300m^3] & [Re-Bar 54 T]	21	20-Feb-16 A	08-Mar-16 A	29-Feb-16	23-Mar-16			[Gantt bar for NBC_0200]												
NBC_0210	Top Slab- Waterproofing & RC construction [Concrete 180m^3] & [Re-Bar 42.7 T]	24	17-Mar-16 A	01-Apr-16 A	26-Apr-16	25-May-16			[Gantt bar for NBC_0210]												
NBC_0220	Construction of flood light footing [2 nos.]	12	29-Mar-16 A	01-Apr-16 A	26-May-16	08-Jun-16			[Gantt bar for NBC_0220]												
NBC_0230	Reinstatement and installation of flood light [2nos.]	6	29-Mar-16 A	01-Nov-16	31-Mar-16	07-Apr-16	-21	0	[Gantt bar for NBC_0230]												
NBC_0240	Backfilling for Northern Basketball Court	12	05-May-16 A	04-Nov-16	05-May-16	19-May-16	-21	0	[Gantt bar for NBC_0240]												
NBC_0250	Reinstate hard paving of Northern Basketball Court	18	04-Nov-16	25-Nov-16	04-Nov-16	25-Nov-16	-21	0	[Gantt bar for NBC_0250]												
NBC_0260	Reinstate surface coating of Northern Basketball Court	12	25-Nov-16	09-Dec-16	25-Nov-16	09-Dec-16	-21	0	[Gantt bar for NBC_0260]												
NBC_0270	Hand over to LCSD, additional remedial if require	12	09-Dec-16	23-Dec-16	09-Dec-16	23-Dec-16	-21	0	[Gantt bar for NBC_0270]												
NBC_0280	Reinstate road surface on Hennessy Road	70	23-Dec-16	22-Mar-17	23-Dec-16	22-Mar-17	-21	0	[Gantt bar for NBC_0280]												
Southern Basket Ball Court																					
SBC_0010	Phase 1 ELS- Sheet Piles Installation [184n. x 24m]	65	22-Jul-14 A	15-Nov-14 A	09-Jul-15	22-Sep-15			[Gantt bar for SBC_0010]												

- █ Actual Level of Effort
- █ Critical Remaining ...
- Primary Baseline
- ◆ Baseline Milestone
- Actual Work
- ◆ Milestone
- Remaining Work

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)												
SBC_0020	Curtain Grouting and remedial works for sheet piles not reaching to design toe level	15	15-Oct-14 A	15-Nov-14 A	23-Sep-15	12-Oct-15			[Gantt bars for SBC_0020]												
SBC_0030	Bulk Excavation (Removal of hard paving on ground surface) & excavation for layer 1 to	21	09-Oct-14 A	01-Nov-14 A	23-Sep-15	19-Oct-15			[Gantt bars for SBC_0030]												
SBC_0040	Phase 1 ELS- Pumping Test preparation works	15	16-Oct-14 A	08-Nov-14 A	23-Sep-15	12-Oct-15			[Gantt bars for SBC_0040]												
SBC_0050	Phase 1 ELS- Pumping Test	11	17-Nov-14 A	28-Nov-14 A	13-Oct-15	26-Oct-15			[Gantt bars for SBC_0050]												
SBC_0060	Phase 1 ELS- Pumping Test Report Preparation and submission to BD	6	04-Dec-14 A	19-Jan-15 A	27-Oct-15	02-Nov-15			[Gantt bars for SBC_0060]												
SBC_0070	Bulk excavation & layer 2 strut & preloading [800m^3]	28	15-Nov-14 A	17-Dec-14 A	12-Jun-15	16-Jul-15			[Gantt bars for SBC_0070]												
SBC_0080	Bulk excavation & layer 3 strut & preloading [800m^3]	30	18-Dec-14 A	24-Jan-15 A	17-Jul-15	20-Aug-15			[Gantt bars for SBC_0080]												
SBC_0090	Plate load test	6	26-Jan-15 A	31-Jan-15 A	13-Jan-16	19-Jan-16			[Gantt bars for SBC_0090]												
SBC_0100	Temporary Traffic Deck construction	12	10-Jan-15 A	28-Jan-15 A	21-Aug-15	03-Sep-15			[Gantt bars for SBC_0100]												
SBC_0110	Plate load test- Preparation of report & submission to BD	12	12-Feb-15 A	16-Mar-15 A	21-Aug-15	03-Sep-15			[Gantt bars for SBC_0110]												
SBC_0120	Base Slab- Waterproofing & RC construction [Concrete 420m^3] & [Re-Bar 25.3 T]	15	04-Sep-15 A	04-Sep-15 A	04-Sep-15	21-Sep-15			[Gantt bars for SBC_0120]												
SBC_0130	Wall- Waterproofing & RC construction [Concrete 280m^3] & [Re-Bar 50.4 T]	21	02-Mar-15 A	17-Mar-15 A	22-Sep-15	17-Oct-15			[Gantt bars for SBC_0130]												
SBC_0140	Top Slab- Waterproofing & RC construction [Concrete 210m^3] & [Re-Bar 50 T]	22	28-Mar-15 A	02-Apr-15 A	19-Oct-15	13-Nov-15			[Gantt bars for SBC_0140]												
SBC_0150	Construction of flood light footing (2 nos.)	7	14-May-15 A	21-May-15 A	01-Jun-15	08-Jun-15			[Gantt bars for SBC_0150]												
SBC_0160	Reinstatement and installation of flood light (2nos.)	3	05-Jun-15 A	05-Jun-15 A	09-Jun-15	11-Jun-15			[Gantt bars for SBC_0160]												
SBC_0170	Backfilling for Southern Basketball Court	6	18-May-15 A	16-Jun-15 A	12-Jun-15	18-Jun-15			[Gantt bars for SBC_0170]												
SBC_0180	Reinstate hard paving of Southern Basketball Court	9	16-Jun-15 A	18-Jun-15 A	02-Jul-15	13-Jul-15			[Gantt bars for SBC_0180]												
SBC_0190	Reinstate surface coating of Southern Basketball Court	9	20-Jun-15 A	29-Jun-15 A	13-Jul-15	23-Jul-15			[Gantt bars for SBC_0190]												
SBC_0200	Hand over to LCSD, additional remedial if require	12	30-Jun-15 A	11-Aug-15 A	23-Jul-15	06-Aug-15			[Gantt bars for SBC_0200]												
Children's Play Area																					
CPA_0010	Phase 1 ELS- Sheet Piles Installation [123 No. x 24m]	65	22-Jul-14 A	15-Nov-14 A	31-Mar-15	22-Jun-15			[Gantt bars for CPA_0010]												
CPA_0020	Curtain Grouting and remedial works for sheet piles not reaching to design toe level	15	15-Oct-14 A	15-Nov-14 A	23-Jun-15	10-Jul-15			[Gantt bars for CPA_0020]												
CPA_0030	Phase 1 ELS- Pumping Test preparation works	15	16-Oct-14 A	08-Nov-14 A	23-Jun-15	10-Jul-15			[Gantt bars for CPA_0030]												
CPA_0040	Bulk Excavation (Removal of hard paving on ground surface) & excavation for layer 1 to	32	27-Oct-14 A	02-Dec-14 A	11-Jul-15	17-Aug-15			[Gantt bars for CPA_0040]												
CPA_0050	Phase 1 ELS- Pumping Test	11	17-Nov-14 A	28-Nov-14 A	11-Jul-15	23-Jul-15			[Gantt bars for CPA_0050]												
CPA_0060	Phase 1 ELS- Pumping Test Report Preparation and submission to BD	6	04-Dec-14 A	19-Jan-15 A	24-Jul-15	30-Jul-15			[Gantt bars for CPA_0060]												
CPA_0070	Bulk excavation & layer 2 strut & preloading to -1.3 mPD [680m^3]	30	18-Dec-14 A	24-Jan-15 A	18-Aug-15	21-Sep-15			[Gantt bars for CPA_0070]												
CPA_0080	Play's Area Temporary Traffic Deck construction	12	10-Jan-15 A	28-Jan-15 A	22-Sep-15	07-Oct-15			[Gantt bars for CPA_0080]												
CPA_0090	Bulk excavation & layer 3 strut & preloading [680m^3]	40	09-Feb-15 A	28-Feb-15 A	08-Oct-15	24-Nov-15			[Gantt bars for CPA_0090]												
CPA_0100	Bulk excavation & layer 4 strut & preloading [680m^3]	50	01-Mar-15 A	27-Mar-15 A	25-Nov-15	25-Jan-16			[Gantt bars for CPA_0100]												
CPA_0110	Plate load test	6	30-Mar-15 A	02-Apr-15 A	26-Jan-16	01-Feb-16			[Gantt bars for CPA_0110]												
CPA_0120	Plate load test- Preparation of report & submission to BD	12	08-Apr-15 A	23-May-15 A	02-Feb-16	18-Feb-16			[Gantt bars for CPA_0120]												
CPA_0130	Base Slab- Waterproofing & RC construction [Concrete 395m^3] & [Re-Bar 23.8 T]	30	23-Apr-15 A	17-Jul-15 A	19-Feb-16	24-Mar-16			[Gantt bars for CPA_0130]												
CPA_0140	Wall- Waterproofing & RC construction [Concrete 210m^3] & [Re-Bar 37.8 T]	18	18-Jun-15 A	06-Aug-15 A	08-Jul-15	28-Jul-15			[Gantt bars for CPA_0140]												
CPA_0150	Top Slab- Waterproofing & RC construction [Concrete 185m^3] & [Re-Bar 43.8 T]	20	07-Aug-15 A	11-Sep-15 A	29-Aug-15	22-Sep-15			[Gantt bars for CPA_0150]												
CPA_0160	Ventilation Shaft Below Ground- Waterproofing & RC construction [Concrete 35m^3] & [20	22-Aug-15 A	14-Sep-15 A	14-Sep-15	08-Oct-15			[Gantt bars for CPA_0160]												
CPA_0170	Ventilation Shaft 1.2m Above Ground- Waterproofing & RC construction [Concrete 25m^3]	18	14-Sep-15 A	09-Nov-16	14-Sep-15	06-Oct-15	-190	0	[Gantt bars for CPA_0170]												
CPA_0180	Ventilation Shaft - Waterproofing & RC construction reach +7.40 & +9.50mPD [Concrete	30	10-Nov-16	14-Dec-16	10-Nov-16	14-Dec-16	-190	0	[Gantt bars for CPA_0180]												
CPA_0190	Site cleaning for PlayArea reinstatement & Landscape works	12	15-Dec-16	30-Dec-16	15-Dec-16	30-Dec-16	-190	0	[Gantt bars for CPA_0190]												
CPA_0200	Reinstatement works for Plays Area	66	31-Dec-16	22-Mar-17	31-Dec-16	22-Mar-17	-190	0	[Gantt bars for CPA_0200]												
CPA_0210	Landscape works	66	23-Mar-17	15-Jun-17	23-Mar-17	15-Jun-17	-190	0	[Gantt bars for CPA_0210]												
CPA_0220	Hand over to LCSD, additional remedial if require	48	16-Jun-17	11-Aug-17	16-Jun-17	11-Aug-17	-190	0	[Gantt bars for CPA_0220]												
Johnston Road																					
JnR_0010	All Sheet Piles on JnR & 1st layer mini piles below Tram track completed	0		10-Apr-16 A		30-Jun-16			[Gantt bars for JnR_0010]												
JnR_0020	Phase 2 ELS- Pumping Test 1 for 1st layer	6	17-Mar-16 A	21-Mar-16 A	13-Apr-16	20-Apr-16			[Gantt bars for JnR_0020]												
JnR_0030	Phase 2 ELS- Pumping Test Report for 1st layer Preparation and submission	6	21-Mar-16 A	25-Apr-16 A	20-Apr-16	27-Apr-16			[Gantt bars for JnR_0030]												
JnR_0040	Phase 2 ELS- 1st layer Pumping Test completed & satisfied	0		25-Apr-16 A		25-Apr-16			[Gantt bars for JnR_0040]												
JnR_0050	Bulk excavation & layer 1 strut & preloading [570m^3]	24	30-May-16 A	27-Jun-16 A	07-May-16	04-Jun-16			[Gantt bars for JnR_0050]												
JnR_0060	All grouting and sheet piles achieved to tot level in Johnston Road	0		07-Mar-16 A		24-Jun-16			[Gantt bars for JnR_0060]												

- █ Actual Level of Effort
- █ Critical Remaining ...
- █ Primary Baseline
- █ Actual Work
- █ Remaining Work
- ◆ Baseline Milestone
- ◆ Milestone

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)




Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)											
JnR_0070	Phase 2 ELS- Pumping Test 2 for whole ELS	6	30-Sep-16 A	08-Oct-16 A	12-Sep-16	20-Sep-16			[Gantt bar for JnR_0070]											
JnR_0080	Phase 2 ELS- Pumping Test Report for whole ELS Preparation and submission	6	08-Oct-16 A	15-Oct-16 A	20-Oct-16	26-Oct-16			[Gantt bar for JnR_0080]											
JnR_0090	Phase 2 ELS- Pumping test completed & satisfied	0		15-Oct-16 A		26-Oct-16			[Gantt bar for JnR_0090]											
JnR_0100	Bulk excavation & layer 2 strut & preloading [570m^3]	18	27-Jun-16 A	19-Nov-16	28-Jul-16	17-Aug-16	-275	0	[Gantt bar for JnR_0100]											
JnR_0110	Bulk excavation & layer 3 strut & preloading [570m^3]	18	21-Nov-16	10-Dec-16	21-Nov-16	10-Dec-16	-275	0	[Gantt bar for JnR_0110]											
JnR_0120	Bulk excavation & layer 4 strut & preloading [570m^3]	21	12-Dec-16	07-Jan-17	12-Dec-16	07-Jan-17	-275	0	[Gantt bar for JnR_0120]											
JnR_0130	Bulk excavation to formation level on JnR	0		07-Jan-17		07-Jan-17	-340	0	[Gantt bar for JnR_0130]											
JnR_0140	Sump pit- Waterproofing & RC construction [Concrete 250m^3] & [Re-Bar 15 T]	18	09-Jan-17	01-Feb-17	09-Jan-17	01-Feb-17	-275	0	[Gantt bar for JnR_0140]											
JnR_0150	Base Slab- Waterproofing & RC construction [Concrete 265m^3] & [Re-Bar 16 T]	17	02-Feb-17	21-Feb-17	02-Feb-17	21-Feb-17	-275	0	[Gantt bar for JnR_0150]											
JnR_0160	Wall- Waterproofing & RC construction [Concrete 70m^3] & [Re-Bar 12.6 T]	18	22-Feb-17	14-Mar-17	22-Feb-17	14-Mar-17	-275	0	[Gantt bar for JnR_0160]											
JnR_0170	Top Slab- Waterproofing & RC construction [Concrete 125m^3] & [Re-Bar 29.6 T]	18	15-Mar-17	05-Apr-17	15-Mar-17	05-Apr-17	-275	0	[Gantt bar for JnR_0170]											
JnR_0180	RC structure completed on JnR	0		05-Apr-17		05-Apr-17	-317	0	[Gantt bar for JnR_0180]											
JnR_0190	Removal of temporary traffic decking ,backfill & road reinstatement on JNR	60	06-Apr-17	21-Jun-17	06-Apr-17	21-Jun-17	-92	0	[Gantt bar for JnR_0190]											
Johnston Road North Footpath (TTM Stage 1, 2, 2A & 2B)																				
JnR.NFP_0010	Liaison, review & acceptance for TTM Stage 1	54	14-Apr-14 A	21-Jun-14 A	31-Mar-15	08-Jun-15			[Gantt bar for JnR.NFP_0010]											
JnR.NFP_0020	Implementation of TTM Stage 1	3	28-Jun-14 A	02-Jul-14 A	09-Jun-15	11-Jun-15			[Gantt bar for JnR.NFP_0020]											
JnR.NFP_0030	Phase 2 ELS- Sheet Piles Installation [30no. x 24m]	12	28-Apr-15 A	09-May-15 A	31-Mar-15	17-Apr-15			[Gantt bar for JnR.NFP_0030]											
JnR.NFP_0040	Curtain Grouting and remedial works for sheet piles not reaching to design toe level	6	01-Jun-15 A	12-Jun-15 A	01-Jun-15	06-Jun-15			[Gantt bar for JnR.NFP_0040]											
JnR.NFP_0050	Installation of temporary traffic decking	6	22-Jun-15 A	21-Jul-15 A	04-Jul-15	10-Jul-15			[Gantt bar for JnR.NFP_0050]											
JnR.NFP_0060	Sheet piles & Traffic decking completed on North Footpath for TTM Stage 3	0		21-Jul-15 A		01-Aug-15			[Gantt bar for JnR.NFP_0060]											
Johnston Road Eastbound carriageway																				
Johnston Road Eastbound carriageway North Side (TTM Stage 3)																				
JnR.EBC.NS_0010	Implementation of TTM 3	3	13-Mar-15 A	14-Mar-15 A	17-Sep-15	19-Sep-15			[Gantt bar for JnR.EBC.NS_0010]											
JnR.EBC.NS_0020	Phase 2 ELS- Sheet Piles Installation [25no. x 24m]	12	27-Jul-15 A	05-Aug-15 A	07-Aug-15	20-Aug-15			[Gantt bar for JnR.EBC.NS_0020]											
JnR.EBC.NS_0030	Curtain Grouting and remedial works for sheet piles not reaching to design toe level	6	03-Aug-15 A	20-Aug-15 A	14-Aug-15	20-Aug-15			[Gantt bar for JnR.EBC.NS_0030]											
JnR.EBC.NS_0040	Installation of temporary traffic decking	6	21-Aug-15 A	31-Aug-15 A	18-Sep-15	25-Sep-15			[Gantt bar for JnR.EBC.NS_0040]											
JnR.EBC.NS_0050	Sheet Piles & Traffic decking completed on Eastbound Carriageway North Side for TTM	0		31-Aug-15 A		25-Sep-15			[Gantt bar for JnR.EBC.NS_0050]											
Johnston Road Eastbound carriageway South Side (TTM Stage 4 & 5)																				
JnR.EBC.SS_0010	Implementation of TTM 4	3	31-Aug-15 A	01-Sep-15 A	31-Aug-15	02-Sep-15			[Gantt bar for JnR.EBC.SS_0010]											
JnR.EBC.SS_0020	Phase 2 ELS- Sheet Piles Installation [33no. x 24m]	9	02-Oct-15 A	14-Jan-16 A	04-Nov-15	13-Nov-15			[Gantt bar for JnR.EBC.SS_0020]											
JnR.EBC.SS_0030	Curtain Grouting and remedial works for sheet piles not reaching to design toe level	6	29-Oct-15 A	04-Jan-16 A	05-Jan-16	12-Jan-16			[Gantt bar for JnR.EBC.SS_0030]											
JnR.EBC.SS_0040	Sheet pile completed on Eastbound Carriageway South Side	0		14-Jan-16 A		07-Apr-16			[Gantt bar for JnR.EBC.SS_0040]											
JnR.EBC.SS_0050	Coring for minipile No. 1 to reach -56mPD [60m]	8	18-Jan-16 A	27-Jan-16 A	11-Feb-16	19-Feb-16			[Gantt bar for JnR.EBC.SS_0050]											
JnR.EBC.SS_0060	Installation of Re-Bar for minipile No.1 [4x60m T50, 3.7Ton]	5	04-Feb-16 A	04-Feb-16 A	20-Feb-16	25-Feb-16			[Gantt bar for JnR.EBC.SS_0060]											
JnR.EBC.SS_0070	Grouting for minipile No.1	1	05-Feb-16 A	05-Feb-16 A	26-Feb-16	26-Feb-16			[Gantt bar for JnR.EBC.SS_0070]											
JnR.EBC.SS_0080	Coring for minipile No. 2 to reach -56mPD [60m]	8	28-Jan-16 A	02-Feb-16 A	20-Feb-16	29-Feb-16			[Gantt bar for JnR.EBC.SS_0080]											
JnR.EBC.SS_0090	Installation of Re-Bar for minipile No.2 [4x60m T50, 3.7Ton]	5	03-Feb-16 A	04-Feb-16 A	01-Mar-16	05-Mar-16			[Gantt bar for JnR.EBC.SS_0090]											
JnR.EBC.SS_0100	Grouting for minipile No.2	1	05-Feb-16 A	05-Feb-16 A	07-Mar-16	07-Mar-16			[Gantt bar for JnR.EBC.SS_0100]											
Johnston Road Tram Tracks (TTM Stage 3)																				
JnR.TT_0010	Implementation of TTM 3	3	13-Mar-15 A	14-Mar-15 A	17-Sep-15	19-Sep-15			[Gantt bar for JnR.TT_0010]											
JnR.TT_0030	1st layer grouting below tram track (NTH) to -6mPD 28no. 800mm C/C [NTH]	24	15-May-15 A	04-Jun-15 A	15-Jun-15	14-Jul-15			[Gantt bar for JnR.TT_0030]											
JnR.TT_0040	1st layer of mini piles below tram tracks completed	0		10-Apr-16 A		30-Jun-16			[Gantt bar for JnR.TT_0040]											
JnR.TT_0050	Expose concrete surface by Tramway Sub-Con	3	16-Mar-15 A	18-Mar-15 A	22-Oct-15	24-Oct-15			[Gantt bar for JnR.TT_0050]											
JnR.TT_0060	Installation of Steel Beam	4	18-Mar-15 A	24-Apr-15 A	22-Oct-15	26-Oct-15			[Gantt bar for JnR.TT_0060]											
JnR.TT_0070	Leveling of steel Beam by Tramway Sub-Con (NTH)	4	24-Apr-15 A	24-Apr-15 A	09-Jun-15	12-Jun-15			[Gantt bar for JnR.TT_0070]											
JnR.TT_0080	Installation of temporary steel decking on tram track	4	25-Apr-15 A	23-May-15 A	09-Jun-15	12-Jun-15			[Gantt bar for JnR.TT_0080]											
JnR.TT_0090	Expose concrete/ fill below tram track [60m^3]	24	25-Apr-15 A	23-May-15 A	13-Jun-15	13-Jul-15			[Gantt bar for JnR.TT_0090]											
JnR.TT_0100	Installation of Re-bars [Re-Bars 7.6T]	12	27-Apr-15 A	23-May-15 A	14-Jul-15	27-Jul-15			[Gantt bar for JnR.TT_0100]											
JnR.TT_0110	Concreting for concrete decking below tram track [Concrete 60m^3]	6	28-Apr-15 A	23-May-15 A	28-Jul-15	03-Aug-15			[Gantt bar for JnR.TT_0110]											

- █ Actual Level of Effort
- █ Critical Remaining ...
- █ Primary Baseline
- █ Actual Work
- █ Remaining Work
- ◆ Baseline Milestone
- ◆ Milestone

**Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)**

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)															
JnR.TT_0120	Reinstate the tram track surface	6	25-May-15 A	06-Jun-15 A	13-Aug-15	20-Aug-15			[Gantt bar for JnR.TT_0120]															
JnR.TT_0130	Tram track concrete decking & reinstatement works completed ready for Implementator	0		06-Jun-15 A		20-Aug-15			[Gantt bar for JnR.TT_0130]															
JnR.TT_0140	2nd layer grouting and pipe piles below tram track to -17mPD (16m) 50no. x 324mm dia	12	01-Aug-16 A	09-Nov-16	01-Aug-16	13-Aug-16	-275	0	[Gantt bar for JnR.TT_0140]															
Johnston Road Westbound carriageway (TTM Stage 5)																								
JnR.WBC_0010	Implementation of TTM Stage 5	3	11-Aug-15 A	12-Aug-15 A	23-Oct-15	26-Oct-15			[Gantt bar for JnR.WBC_0010]															
JnR.WBC_0020	Trial Trench	12	11-Aug-15 A	18-Aug-15 A	27-Oct-15	09-Nov-15			[Gantt bar for JnR.WBC_0020]															
JnR.WBC_0030	Phase 2 ELS- Sheet Piles Installation [20no. x 24m]	6	13-Feb-16 A	07-Mar-16 A	15-Mar-16	21-Mar-16			[Gantt bar for JnR.WBC_0030]															
JnR.WBC_0040	Curtain Grouting and remedial works for sheet piles not reaching to design toe level	3	22-Feb-16 A	16-Mar-16 A	09-Apr-16	13-Apr-16			[Gantt bar for JnR.WBC_0040]															
JnR.WBC_0050	Sheet piles completed on Westbound carriageway	0		16-Mar-16 A		13-Apr-16			[Gantt bar for JnR.WBC_0050]															
JnR.WBC_0060	Coring for minipile No. 3 to reach -56mPD [60m]	8	29-Mar-16 A	01-Apr-16 A	08-Apr-16	16-Apr-16			[Gantt bar for JnR.WBC_0060]															
JnR.WBC_0070	Installation of Re-Bar for minipile No.3 [4x 60m T50, 3.7Ton]	5	15-Apr-16 A	15-Apr-16 A	16-May-16	21-May-16			[Gantt bar for JnR.WBC_0070]															
JnR.WBC_0080	Grouting for minipile No.3	1	18-Apr-16 A	20-Apr-16 A	21-May-16	23-May-16			[Gantt bar for JnR.WBC_0080]															
JnR.WBC_0090	Coring for minipile No. 4 to reach -56mPD [60m]	8	01-Apr-16 A	11-Apr-16 A	16-May-16	25-May-16			[Gantt bar for JnR.WBC_0090]															
JnR.WBC_0100	Installation of Re-Bar for minipile No.4 [4x 60m T50, 3.7Ton]	5	16-Apr-16 A	16-Apr-16 A	25-May-16	31-May-16			[Gantt bar for JnR.WBC_0100]															
JnR.WBC_0110	Grouting for minipile No.4	1	19-Apr-16 A	20-Apr-16 A	31-May-16	01-Jun-16			[Gantt bar for JnR.WBC_0110]															
JnR.WBC_0120	Re-Bar Installation for minipile location	4	15-Apr-16 A	17-Apr-16 A	01-Jun-16	06-Jun-16			[Gantt bar for JnR.WBC_0120]															
JnR.WBC_0130	Cast Concrete minipile location	2	20-Apr-16 A	22-Apr-16 A	05-Jul-16	06-Jul-16			[Gantt bar for JnR.WBC_0130]															
Johnston Road Westbound carriageway East Side (TTM Stage 2A)																								
JnR.WBC.ES_0010	Implementation of TTM Stage 2A	3	18-Dec-14 A	20-Dec-14 A	12-Jun-15	15-Jun-15			[Gantt bar for JnR.WBC.ES_0010]															
JnR.WBC.ES_0020	Expose UU	12	22-Dec-14 A	07-Jan-15 A	16-Jun-15	30-Jun-15			[Gantt bar for JnR.WBC.ES_0020]															
JnR.WBC.ES_0030	UU diversion on JnR Westbound Carriageway East Side	24	08-Jan-15 A	04-Feb-15 A	02-Jul-15	29-Jul-15			[Gantt bar for JnR.WBC.ES_0030]															
JnR.WBC.ES_0040	Installation of temporary traffic decking	3	05-Feb-15 A	07-Feb-15 A	30-Jul-15	01-Aug-15			[Gantt bar for JnR.WBC.ES_0040]															
JnR.WBC.ES_0050	Traffic decking completed on Westbound Carriageway East Side for TTM Stage 2B	0		07-Feb-15 A		01-Aug-15			[Gantt bar for JnR.WBC.ES_0050]															
Johnston Road Westbound carriageway West Side (TTM Stage 2B)																								
JnR.WBC.WS_0010	Implementation of TTM Stage 2B	3	09-Feb-15 A	11-Feb-15 A	03-Aug-15	05-Aug-15			[Gantt bar for JnR.WBC.WS_0010]															
JnR.WBC.WS_0020	Expose UU	12	12-Feb-15 A	28-Feb-15 A	06-Aug-15	19-Aug-15			[Gantt bar for JnR.WBC.WS_0020]															
JnR.WBC.WS_0030	UU diversion on JnR Westbound Carriageway West Side	18	02-Mar-15 A	21-Mar-15 A	31-Mar-15	24-Apr-15			[Gantt bar for JnR.WBC.WS_0030]															
JnR.WBC.WS_0040	UU diversion on JnR Westbound Carriageway Completed	0		21-Mar-15 A		24-Apr-15			[Gantt bar for JnR.WBC.WS_0040]															
JnR.WBC.WS_0050	Installation of temporary traffic decking	6	23-Mar-15 A	28-Mar-15 A	30-Apr-16	07-May-16			[Gantt bar for JnR.WBC.WS_0050]															
JnR.WBC.WS_0060	Traffic decking completed on Westbound Carriageway West Side for TTM Stage 3	0		28-Mar-15 A		07-May-16			[Gantt bar for JnR.WBC.WS_0060]															
Johnston Road South Footpath (TTM 4)																								
JnR.SFP_0010	Implementation of TTM 4	3	23-Jun-15 A	23-Jun-15 A	08-Aug-15	11-Aug-15			[Gantt bar for JnR.SFP_0010]															
JnR.SFP_0020	Expose UU	12	23-Jun-15 A	06-Jul-15 A	12-Aug-15	25-Aug-15			[Gantt bar for JnR.SFP_0020]															
JnR.SFP_0030	UU diversion	9	23-Jun-15 A	06-Jul-15 A	26-Aug-15	04-Sep-15			[Gantt bar for JnR.SFP_0030]															
JnR.SFP_0040	Phase 2 ELS- Sheet Piles Installation [15no. x 24m]	6	05-Dec-15 A	15-Dec-15 A	05-Jan-16	11-Jan-16			[Gantt bar for JnR.SFP_0040]															
JnR.SFP_0050	Curtain Grouting and remedial works for sheet piles not reaching to design toe level	3	16-Dec-15 A	24-Dec-15 A	12-Jan-16	14-Jan-16			[Gantt bar for JnR.SFP_0050]															
JnR.SFP_0060	Installation of Temporary Traffic decking	6	13-Jan-16 A	25-Jan-16 A	08-Mar-16	14-Mar-16			[Gantt bar for JnR.SFP_0060]															
JnR.SFP_0070	Sheet Piles & Traffic decking completed on South Footpath for TTM Stage 5	0		25-Jan-16 A		07-Apr-16			[Gantt bar for JnR.SFP_0070]															
H15 Break Through Works																								
H15_0010	Installation protection measurement for break through	3	10-Apr-17	12-Apr-17	10-Apr-17	12-Apr-17	-260	0	[Gantt bar for H15_0010]															
H15_0020	Breaking out to H15 - Form opening, core holes & wire cut, 60 no. x 0.9m x 0.9m x 1m t	48	13-Apr-17	14-Jun-17	13-Apr-17	14-Jun-17	-260	0	[Gantt bar for H15_0020]															
H15_0030	Breaking out to H15 - Installation of temporary steel propping	30	22-Apr-17	29-May-17	22-Apr-17	29-May-17	-247	13	[Gantt bar for H15_0030]															
H15_0040	Breaking out to H15 - Construct the portal frame	12	15-Jun-17	28-Jun-17	15-Jun-17	28-Jun-17	-260	0	[Gantt bar for H15_0040]															
H15_0050	Demolish the propping steel members	2	29-Jun-17	30-Jun-17	29-Jun-17	30-Jun-17	-260	0	[Gantt bar for H15_0050]															
Cost Centre B: Part A Works, ABWF Works for the New Subway																								
ABWF_0010	Preparation works for Fire Shutter on GL-L	6	03-May-16 A	09-May-16 A	19-Dec-16	24-Dec-16			[Gantt bar for ABWF_0010]															
ABWF_0020	Installation of Fire Shutter on GL-L	3	06-Apr-17	08-Apr-17	06-Apr-17	08-Apr-17	-260	0	[Gantt bar for ABWF_0020]															
ABWF_0030	Preparation works for Security Shutter on GL-L	6	03-May-16 A	09-May-16 A	19-Dec-16	24-Dec-16			[Gantt bar for ABWF_0030]															
ABWF_0040	Installation of Security Shutter on GL-L	3	06-Apr-17	08-Apr-17	06-Apr-17	08-Apr-17	-260	0	[Gantt bar for ABWF_0040]															

- █ Actual Level of Effort
- █ Critical Remaining ...
- Primary Baseline
- ◆ Baseline Milestone
- Actual Work
- ◆ Milestone
- Remaining Work

**Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)**

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)											
ABWF_0050	Preparation works for Flood Gate on GL-L	6	03-May-16 A	09-May-16 A	19-Dec-16	24-Dec-16			[Gantt bars for ABWF_0050]											
ABWF_0060	Installation for Flood Gate on GL-L	3	06-Apr-17	08-Apr-17	06-Apr-17	08-Apr-17	-260	0	[Gantt bars for ABWF_0060]											
ABWF_0070	Completion of Flood Gate, Fire Shutter & Security Shutter on GL-L	0		08-Apr-17		08-Apr-17	-317	1	[Gantt bars for ABWF_0070]											
ABWF_0080	Remaining ABWF, finishing & Site cleaning works	90	07-Sep-17	27-Dec-17	07-Sep-17	27-Dec-17	-247	0	[Gantt bars for ABWF_0080]											
ABWF Works - Degree 1																				
ABWF.D1_0010	Site Cleaning & dry the internal of Structure & building	72	19-Dec-16 A	23-May-17	19-Dec-16	18-Mar-17	-233	0	[Gantt bars for ABWF.D1_0010]											
ABWF.D1_0020	Installation of blockwalls & partition wall except on plant access route	72	19-Dec-16 A	10-Jun-17	19-Dec-16	18-Mar-17	-247	0	[Gantt bars for ABWF.D1_0020]											
ABWF.D1_0030	Apply Plastering, undercoat, painting, floor screeding including plinths and upstands	72	22-Feb-17 A	10-Jun-17	22-Feb-17	24-May-17	-82	0	[Gantt bars for ABWF.D1_0030]											
ABWF.D1_0040	Forming equipment delivery routes and access openings for DC or Interface Contractors	72	06-Apr-17	06-Jul-17	06-Apr-17	06-Jul-17	-104	0	[Gantt bars for ABWF.D1_0040]											
ABWF.D1_0050	Install Cast-in items, subframe; Form niches, recesses & box outs; Install cable troughs, i	72	06-Apr-17	06-Jul-17	06-Apr-17	06-Jul-17	-104	0	[Gantt bars for ABWF.D1_0050]											
ABWF.D1_0060	Preparation, submission and approval of Structure as-built survey	72	06-Apr-17	06-Jul-17	06-Apr-17	06-Jul-17	-104	0	[Gantt bars for ABWF.D1_0060]											
ABWF.D1_0070	Form Structural & blockwork E&M openings & preparation of survey	72	06-Apr-17	06-Jul-17	06-Apr-17	06-Jul-17	-104	0	[Gantt bars for ABWF.D1_0070]											
ABWF.D1_0080	Installation of movement joints & stitch strips	72	06-Apr-17	06-Jul-17	06-Apr-17	06-Jul-17	-104	0	[Gantt bars for ABWF.D1_0080]											
ABWF.D1_0090	Form escalator zones & pits complete; survey reference lines for acceptance	72	06-Apr-17	06-Jul-17	06-Apr-17	06-Jul-17	-104	0	[Gantt bars for ABWF.D1_0090]											
ABWF.D1_0100	Installation of Earthing mat, earthing rods & earthing pits, test & acceptance	72	06-Apr-17	06-Jul-17	06-Apr-17	06-Jul-17	-104	0	[Gantt bars for ABWF.D1_0100]											
ABWF.D1_0110	Installation of underground pipe work including manholes, ductworks & drawpits	72	06-Apr-17	06-Jul-17	06-Apr-17	06-Jul-17	-104	0	[Gantt bars for ABWF.D1_0110]											
ABWF Works - Degree 2																				
ABWF.D2_0010	Permanent door frames installed with temporary doors & locks	42	10-Jun-17	31-Jul-17	10-Jun-17	31-Jul-17	-241	0	[Gantt bars for ABWF.D2_0010]											
ABWF.D2_0020	Installation of Floor finishes & wall tiling in plant rooms for Designated Contractors	36	24-Jun-17	07-Aug-17	24-Jun-17	07-Aug-17	-247	0	[Gantt bars for ABWF.D2_0020]											
ABWF.D2_0030	Install Glazing & Balustrade support	12	10-Jun-17	24-Jun-17	10-Jun-17	24-Jun-17	-247	0	[Gantt bars for ABWF.D2_0030]											
ABWF.D2_0040	Install Metal staircases, cat-ladders & catwalks	42	10-Jun-17	31-Jul-17	10-Jun-17	31-Jul-17	-244	0	[Gantt bars for ABWF.D2_0040]											
ABWF.D2_0050	Install External louvers	42	10-Jun-17	31-Jul-17	10-Jun-17	31-Jul-17	-244	0	[Gantt bars for ABWF.D2_0050]											
ABWF.D2_0060	Install Framework for final finishes	42	10-Jun-17	31-Jul-17	10-Jun-17	31-Jul-17	-244	0	[Gantt bars for ABWF.D2_0060]											
ABWF.D2_0070	Water tightness testing to water tanks & acceptance	42	24-May-17	13-Jul-17	24-May-17	13-Jul-17	-230	0	[Gantt bars for ABWF.D2_0070]											
ABWF Works - Degree 3																				
ABWF.D3_0010	Inatall & apply all remaining finishes including permanent doors, ironmongery	27	07-Aug-17	07-Sep-17	07-Aug-17	07-Sep-17	-247	0	[Gantt bars for ABWF.D3_0010]											
ABWF.D3_0011	Installation of VE Panel [591m^2]	33	31-Jul-17	07-Sep-17	31-Jul-17	07-Sep-17	-157	0	[Gantt bars for ABWF.D3_0011]											
ABWF.D3_0012	Installation of Ceiling Panel [565 m^2]	33	31-Jul-17 A	04-Sep-17	31-Jul-17	07-Sep-17	-154	3	[Gantt bars for ABWF.D3_0012]											
ABWF.D3_0013	Installation of floor finishing [565 m^2]	27	07-Aug-17	07-Sep-17	07-Aug-17	07-Sep-17	-157	0	[Gantt bars for ABWF.D3_0013]											
ABWF.D3_0020	Install Balustrade	27	07-Aug-17	07-Sep-17	07-Aug-17	07-Sep-17	-247	0	[Gantt bars for ABWF.D3_0020]											
ABWF.D3_0030	Install Signage hangers & supports	30	31-Jul-17	04-Sep-17	31-Jul-17	04-Sep-17	-244	0	[Gantt bars for ABWF.D3_0030]											
ABWF.D3_0040	Install smoke barriers	30	31-Jul-17	04-Sep-17	31-Jul-17	04-Sep-17	-244	0	[Gantt bars for ABWF.D3_0040]											
ABWF.D3_0050	Apply Acoustic treatment	30	31-Jul-17	04-Sep-17	31-Jul-17	04-Sep-17	-244	0	[Gantt bars for ABWF.D3_0050]											
ABWF.D3_0060	Install Louvres & grilles	30	31-Jul-17	04-Sep-17	31-Jul-17	04-Sep-17	-244	0	[Gantt bars for ABWF.D3_0060]											
ABWF.D3_0070	Seal All openings & Penetrations	30	14-Jul-17	17-Aug-17	14-Jul-17	17-Aug-17	-230	0	[Gantt bars for ABWF.D3_0070]											
C: Building Services																				
Design, Shop Drawings, Materials & Equipments Submission and Approval																				
BS.DS_0010	BS Works- Preparation and submission for detailed design of BS works	128	14-Apr-14 A	18-Sep-14 A	31-Mar-15	04-Sep-15			[Gantt bars for BS.DS_0010]											
BS.DS_0020	BS Works- Review and approval for detailed design of BS works	12	19-Sep-14 A	04-Oct-14 A	05-Sep-15	18-Sep-15			[Gantt bars for BS.DS_0020]											
BS.DS_0030	BS Works- Preparation and re-submission for detailed design of BS works (If require)	12	06-Oct-14 A	18-Oct-14 A	19-Sep-15	05-Oct-15			[Gantt bars for BS.DS_0030]											
BS.DS_0040	BS Works- Review and approval for detailed design of BS works (If require)	12	20-Oct-14 A	01-Nov-14 A	06-Oct-15	19-Oct-15			[Gantt bars for BS.DS_0040]											
BS.DS_0050	BS Works- Contractor prepare & submit the propose suppliers & model types of major E	128	14-Apr-14 A	18-Sep-14 A	31-Mar-15	04-Sep-15			[Gantt bars for BS.DS_0050]											
BS.DS_0060	BS Works- Review & approval the propose suppliers & model types of major BS equipm	12	19-Sep-14 A	04-Oct-14 A	05-Sep-15	18-Sep-15			[Gantt bars for BS.DS_0060]											
BS.DS_0070	BS Works- Contractor prepare & re-submit propose suppliers & model types of major B'	12	06-Oct-14 A	18-Oct-14 A	19-Sep-15	05-Oct-15			[Gantt bars for BS.DS_0070]											
BS.DS_0080	BS Works- Review the propose suppliers & model types of major BS equipment & mater	12	20-Oct-14 A	01-Nov-14 A	06-Oct-15	19-Oct-15			[Gantt bars for BS.DS_0080]											
BS.DS_0090	BS Works- Preparation and submission of BS shop drawings	32	03-Nov-14 A	09-Dec-14 A	20-Oct-15	26-Nov-15			[Gantt bars for BS.DS_0090]											
BS.DS_0100	BS Works- Review and approval of BS shop drawings	12	10-Dec-14 A	23-Dec-14 A	27-Nov-15	10-Dec-15			[Gantt bars for BS.DS_0100]											
BS.DS_0110	BS Works- Preparation and re-submission of BS shop drawings (If require)	12	24-Dec-14 A	09-Jan-15 A	11-Dec-15	24-Dec-15			[Gantt bars for BS.DS_0110]											
BS.DS_0120	BS Works- Review and approval of BS shop drawings (If require)	12	10-Jan-15 A	23-Jan-15 A	28-Dec-15	11-Jan-16			[Gantt bars for BS.DS_0120]											

- █ Actual Level of Effort
- █ Critical Remaining ...
- █ Primary Baseline
- █ Actual Work
- █ Remaining Work
- ◆ Baseline Milestone
- ◆ Milestone

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart (2014-2018)												
BS_DS_0130	Exchange of Design Information with Designated and Interfacing Contractors	100	24-Jan-15 A	30-May-15 A	31-Jul-15	27-Nov-15			[Gantt Chart Data]												
Procurement and Delivery of Materials and Equipments																					
BS_PD_0010	All Major building service equipments & materials - Manufacture & fabrication - Procurement	50	03-Nov-14 A	02-Jan-15 A	20-Oct-15	17-Dec-15			[Gantt Chart Data]												
BS_PD_0020	Others Major building service equipments & materials - Place order	95	03-Jan-15 A	02-May-15 A	18-Dec-15	18-Apr-16			[Gantt Chart Data]												
BS_PD_0030	Others Major building service equipments & materials - Manufacture & fabrication	90	04-May-15 A	19-Aug-15 A	24-Sep-15	14-Jan-16			[Gantt Chart Data]												
BS_PD_0040	Others Major building service equipments & materials - Factory acceptance testing	24	20-Aug-15 A	16-Sep-15 A	01-Feb-16	02-Mar-16			[Gantt Chart Data]												
BS_PD_0050	Others Major building service equipments & materials - Remedial works (If require)	36	17-Sep-15 A	31-Oct-15 A	03-Mar-16	18-Apr-16			[Gantt Chart Data]												
BS_PD_0060	Others Major building service equipments & materials - Factory acceptance (If require)	24	02-Nov-15 A	18-Nov-15 A	19-Apr-16	18-May-16			[Gantt Chart Data]												
BS_PD_0070	Others Major building service equipments & materials - Delivery to site/ ECS Room	90	30-Nov-15 A	19-Mar-16 A	19-May-16	02-Sep-16			[Gantt Chart Data]												
BS_PD_0080	Air Handling Unit - Place Order	95	03-Jan-15 A	05-Jan-15 A	18-Dec-15	18-Apr-16			[Gantt Chart Data]												
BS_PD_0090	Air Handling Unit - Manufacture & fabrication	90	04-May-15 A	19-Aug-15 A	31-Jul-15	16-Nov-15			[Gantt Chart Data]												
BS_PD_0100	Air Handling Unit - Factory acceptance testing	24	20-Aug-15 A	16-Sep-15 A	25-Feb-16	23-Mar-16			[Gantt Chart Data]												
BS_PD_0110	Air Handling Unit - Remedial works (If require)	36	17-Sep-15 A	31-Oct-15 A	24-Mar-16	10-May-16			[Gantt Chart Data]												
BS_PD_0120	Air Handling Unit - Factory acceptance testing (If require)	24	02-Nov-15 A	28-Nov-15 A	11-May-16	08-Jun-16			[Gantt Chart Data]												
BS_PD_0130	Air Handling Unit - Delivery to site/ ECS Room	90	30-Nov-15 A	19-Mar-16 A	10-Jun-16	24-Sep-16			[Gantt Chart Data]												
BS_PD_0140	In-line Centrifugal Fan - Place Order	95	03-Jan-15 A	05-Jan-15 A	18-Dec-15	18-Apr-16			[Gantt Chart Data]												
BS_PD_0150	In-line Centrifugal Fan - Manufacture & fabrication	90	04-May-15 A	19-Aug-15 A	31-Jul-15	16-Nov-15			[Gantt Chart Data]												
BS_PD_0160	In-line Centrifugal Fan - Factory acceptance testing	24	20-Aug-15 A	16-Sep-15 A	25-Feb-16	23-Mar-16			[Gantt Chart Data]												
BS_PD_0170	In-line Centrifugal Fan - Remedial works (If require)	36	17-Sep-15 A	31-Oct-15 A	24-Mar-16	10-May-16			[Gantt Chart Data]												
BS_PD_0180	In-line Centrifugal Fan - Factory acceptance testing (If require)	24	02-Nov-15 A	28-Nov-15 A	11-May-16	08-Jun-16			[Gantt Chart Data]												
BS_PD_0190	In-line Centrifugal Fan - Delivery to Site/ ECS Room	90	30-Nov-15 A	19-Mar-16 A	10-Jun-16	24-Sep-16			[Gantt Chart Data]												
BS_PD_0200	Smoke Extraction Fan - Place Order	95	03-Jan-15 A	05-Jan-15 A	18-Dec-15	18-Apr-16			[Gantt Chart Data]												
BS_PD_0210	Smoke Extraction Fan - Manufacture & fabrication	90	04-May-15 A	19-Aug-15 A	31-Jul-15	16-Nov-15			[Gantt Chart Data]												
BS_PD_0220	Smoke Extraction Fan - Factory acceptance testing	24	20-Aug-15 A	16-Sep-15 A	25-Feb-16	23-Mar-16			[Gantt Chart Data]												
BS_PD_0230	Smoke Extraction Fan - Remedial works (If require)	36	17-Sep-15 A	31-Oct-15 A	24-Mar-16	10-May-16			[Gantt Chart Data]												
BS_PD_0240	Smoke Extraction Fan - Factory acceptance testing (If require)	24	02-Nov-15 A	28-Nov-15 A	11-May-16	08-Jun-16			[Gantt Chart Data]												
BS_PD_0250	Smoke Extraction Fan - Delivery to site/ ECS Room	90	30-Nov-15 A	19-Mar-16 A	10-Jun-16	24-Sep-16			[Gantt Chart Data]												
BS_PD_0260	Fan Coil Unit - Place order	95	03-Jan-15 A	05-Jan-15 A	18-Dec-15	18-Apr-16			[Gantt Chart Data]												
BS_PD_0270	Fan Coil Unit - Manufacture & fabrication	90	04-May-15 A	19-Aug-15 A	31-Jul-15	16-Nov-15			[Gantt Chart Data]												
BS_PD_0280	Fan Coil Unit - Factory acceptance testing	24	20-Aug-15 A	16-Sep-15 A	25-Feb-16	23-Mar-16			[Gantt Chart Data]												
BS_PD_0290	Fan Coil Unit - Remedial works (If require)	36	17-Sep-15 A	31-Oct-15 A	24-Mar-16	10-May-16			[Gantt Chart Data]												
BS_PD_0300	Fan Coil Unit - Factory acceptance testing (If require)	24	02-Nov-15 A	28-Nov-15 A	11-May-16	08-Jun-16			[Gantt Chart Data]												
BS_PD_0310	Fan Coil Unit - Delivery to site/ ECS Room	90	30-Nov-15 A	19-Mar-16 A	10-Jun-16	24-Sep-16			[Gantt Chart Data]												
BS_PD_0320	Motorized Smoke & Fire damper - Place order	95	03-Jan-15 A	05-Jan-15 A	18-Dec-15	18-Apr-16			[Gantt Chart Data]												
BS_PD_0330	Motorized Smoke & Fire damper - Manufacture & fabrication	90	04-May-15 A	19-Aug-15 A	31-Jul-15	16-Nov-15			[Gantt Chart Data]												
BS_PD_0340	Motorized Smoke & Fire damper - Factory acceptance testing	24	20-Aug-15 A	16-Sep-15 A	25-Feb-16	23-Mar-16			[Gantt Chart Data]												
BS_PD_0350	Motorized Smoke & Fire damper - Remedial works (If require)	36	17-Sep-15 A	31-Oct-15 A	24-Mar-16	10-May-16			[Gantt Chart Data]												
BS_PD_0360	Motorized Smoke & Fire damper - Factory acceptance testing (If require)	24	02-Nov-15 A	28-Nov-15 A	11-May-16	08-Jun-16			[Gantt Chart Data]												
BS_PD_0370	Motorized Smoke & Fire damper - Delivery to site/ ECS Room	90	30-Nov-15 A	19-Mar-16 A	10-Jun-16	24-Sep-16			[Gantt Chart Data]												
BS_PD_0380	All Major equipment BS equipment & materials - Completed placing orders	0		02-May-15 A		31-Mar-16			[Gantt Chart Data]												
BS_PD_0390	All Major equipment BS equipment & materials - Completed all factory acceptance testing	0		28-Nov-15 A		31-Mar-16			[Gantt Chart Data]												
BS_PD_0400	All Major equipment BS equipment & materials - Completed delivery to ECS room	0		19-Mar-16 A		04-Jun-16			[Gantt Chart Data]												
Installation of Building Services																					
BS_I_0009	Installation of trucking, cable for the whole subway linking between H15 and WAC station	17	22-Feb-17 A	27-Apr-17	22-Feb-17	14-Mar-17	-275	0	[Gantt Chart Data]												
BS_I_0010	Electrical - Within Stn, Distribution equip. 16 nr, cable tray & trunk 420m, lighting fitting 8'	49	31-Oct-16	28-Dec-16	31-Oct-16	28-Dec-16	-181	94	[Gantt Chart Data]												
BS_I_0020	Electrical - Subway, D.eq.82nr, cable tray&trunk 803m, cable 2200m, light fit 91nr, earth	50	27-Apr-17	28-Jun-17	27-Apr-17	28-Jun-17	-275	0	[Gantt Chart Data]												
BS_I_0030	Electrical - Subway, D.eq.82nr, cable tray&trunk 803m, cable 2200m, light fit 91nr, earth	60	28-Jun-17	07-Sep-17	28-Jun-17	07-Sep-17	-275	0	[Gantt Chart Data]												
BS_I_0040	ECS - Within WAC Stn, Grille 6 nr, air duct 115m2, damper 7 nr.	30	27-Apr-17	05-Jun-17	27-Apr-17	05-Jun-17	-261	0	[Gantt Chart Data]												
BS_I_0050	ECS - Subway, Pipe/insul.75m, fan 12nr, grille 45nr, airduct 1106m2, paint 60m2, damp	42	05-Jun-17	25-Jul-17	05-Jun-17	25-Jul-17	-261	0	[Gantt Chart Data]												


- █ Actual Level of Effort
- █ Primary Baseline
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining ...
- ◆ Baseline Milestone
- ◆ Milestone

Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart											
									2014	2015				2016				2017		
BS.I_0060	ECS - Subway, Pipe/insul.75m, fan 12nr, grille 45nr, airduct 1106m2, paint 60m2, dampers	24	25-Jul-17	22-Aug-17	25-Jul-17	22-Aug-17	-261	14	[Gantt bars and milestones for BS.I_0060]											
BS.I_0070	FS Works - Within H15, Pipe 59m, dectector 7 nr, hose reel 1 nr	21	03-Jul-17	26-Jul-17	03-Jul-17	26-Jul-17	-260	0	[Gantt bars and milestones for BS.I_0070]											
BS.I_0080	FS Works - Subway, Pipe 155m, valve 2 nr, detectors 38 nr, hose reel 1 nr, fire extinguishers	21	27-Jul-17	19-Aug-17	27-Jul-17	19-Aug-17	-260	15	[Gantt bars and milestones for BS.I_0080]											
BS.I_0090	Drainage System - Waste - Existing WSC Stn, 35 m pipe, 2 valve, 4 pit, 1 switch/ control	18	27-Apr-17 A	18-May-17	27-Apr-17	20-May-17	-215	0	[Gantt bars and milestones for BS.I_0090]											
BS.I_0100	Drainage System - Waste - Subway, Pipe DI/CI 257+18m, 7 joint, 6 OTC	18	20-May-17 A	07-Jun-17	20-May-17	12-Jun-17	-215	0	[Gantt bars and milestones for BS.I_0100]											
BS.I_0110	Drainage System - Rainwater Discharge, CI pipe, 8+18m above/below ground, 2 manhc	18	12-Jun-17 A	26-Jun-17	12-Jun-17	04-Jul-17	-215	0	[Gantt bars and milestones for BS.I_0110]											
BS.I_0120	Cleansing Water System - Within WAC Station, 137m copper pipe, 3 gate valve, 2 stopc	54	27-Apr-17	04-Jul-17	27-Apr-17	04-Jul-17	-268	0	[Gantt bars and milestones for BS.I_0120]											
BS.I_0130	Cleansing Water System - Subway, 87m copper pipe, 1 gate valve, 1 joint	48	04-Jul-17	29-Aug-17	04-Jul-17	29-Aug-17	-268	0	[Gantt bars and milestones for BS.I_0130]											
BS.I_0140	Installation of Air Handling Unit	110	27-Apr-17	07-Sep-17	27-Apr-17	07-Sep-17	-275	0	[Gantt bars and milestones for BS.I_0140]											
BS.I_0150	Installation of In-line Centrifugal Fan	110	27-Apr-17	07-Sep-17	27-Apr-17	07-Sep-17	-275	0	[Gantt bars and milestones for BS.I_0150]											
BS.I_0160	Installation of Smoke Extraction Fan	110	27-Apr-17	07-Sep-17	27-Apr-17	07-Sep-17	-275	0	[Gantt bars and milestones for BS.I_0160]											
BS.I_0170	Installation of Fan Coil Unit	110	27-Apr-17	07-Sep-17	27-Apr-17	07-Sep-17	-275	0	[Gantt bars and milestones for BS.I_0170]											
BS.I_0180	Installation of Motorized Smoke & Fire damper	110	27-Apr-17	07-Sep-17	27-Apr-17	07-Sep-17	-275	0	[Gantt bars and milestones for BS.I_0180]											
BS.I_0190	Installation & integration of control system	110	27-Apr-17	07-Sep-17	27-Apr-17	07-Sep-17	-275	0	[Gantt bars and milestones for BS.I_0190]											
BS.I_0200	Remaining BS Works	21	07-Sep-17	03-Oct-17	07-Sep-17	03-Oct-17	-272	3	[Gantt bars and milestones for BS.I_0200]											
INF.SAMSp	Interface Access for SAMS, Comms, MCS to All Areas, All Levels and Locations (10-Oct)	0		07-Sep-17		07-Sep-17	-192	0	[Gantt bars and milestones for INF.SAMSp]											
Testing and Commissioning																				
BS.TC_0010	T&C ECS - Tests on Ventilation Fans, Air Balancing, Equipment & System, Control, Noise	24	07-Sep-17	07-Oct-17	07-Sep-17	07-Oct-17	-275	0	[Gantt bars and milestones for BS.TC_0010]											
BS.TC_0020	T&C - SAT of HV Sw Boards/ TX, LV Sw Boards & MCC, Lighting Control, etc.	24	07-Sep-17	07-Oct-17	07-Sep-17	07-Oct-17	-275	0	[Gantt bars and milestones for BS.TC_0020]											
BS.TC_0030	T&C Fire Services - Performance Test/ FH & HR System/ Auto Fire Alarm System	24	07-Sep-17	07-Oct-17	07-Sep-17	07-Oct-17	-275	0	[Gantt bars and milestones for BS.TC_0030]											
BS.TC_0040	T&C Plumbing and Drainage - P&D Pumps, Control System	24	29-Aug-17	26-Sep-17	29-Aug-17	26-Sep-17	-268	0	[Gantt bars and milestones for BS.TC_0040]											
BS.TC_0050	T&C ELV System - Control Systems	24	07-Sep-17	07-Oct-17	07-Sep-17	07-Oct-17	-275	0	[Gantt bars and milestones for BS.TC_0050]											
FSI	FSI - Integrated Test	11	07-Oct-17	20-Oct-17	07-Oct-17	20-Oct-17	-275	0	[Gantt bars and milestones for FSI]											
Statutory Inspection and Approval																				
BS.SIA_0010	Submit BA14 for completion of breakthrough	6	03-Jul-17	08-Jul-17	03-Jul-17	08-Jul-17	-130	0	[Gantt bars and milestones for BS.SIA_0010]											
BS.SIA_0020	BD's acknowledgement letter obtained	24	10-Jul-17	05-Aug-17	10-Jul-17	05-Aug-17	-130	289	[Gantt bars and milestones for BS.SIA_0020]											
BS.SIA_0030	DSD/ WSD Inspection and Connection	24	26-Sep-17	26-Oct-17	26-Sep-17	26-Oct-17	-268	7	[Gantt bars and milestones for BS.SIA_0030]											
BS.SIA_0040	Connection for electricity	12	20-Oct-17	04-Nov-17	20-Oct-17	04-Nov-17	-275	0	[Gantt bars and milestones for BS.SIA_0040]											
BS.SIA_0050	Submit Form 1 and Form 2	1	04-Nov-17	06-Nov-17	04-Nov-17	06-Nov-17	-275	0	[Gantt bars and milestones for BS.SIA_0050]											
BS.SIA_0060	FS Inspection / Re-inspection	12	06-Nov-17	20-Nov-17	06-Nov-17	20-Nov-17	-275	0	[Gantt bars and milestones for BS.SIA_0060]											
BS.SIA_0070	FS Defect Rectification and Approval	12	21-Nov-17	05-Dec-17	21-Nov-17	05-Dec-17	-275	0	[Gantt bars and milestones for BS.SIA_0070]											
BS.SIA_0080	Form 3 Obtained	1	05-Dec-17	06-Dec-17	05-Dec-17	06-Dec-17	-275	0	[Gantt bars and milestones for BS.SIA_0080]											
BS.SIA_0090	BD Inspection/ Re-inspection	6	06-Dec-17	13-Dec-17	06-Dec-17	13-Dec-17	-275	0	[Gantt bars and milestones for BS.SIA_0090]											
BS.SIA_0100	EMSD-RB Pre-Inspection by MTRC Ops Team	1	13-Dec-17	14-Dec-17	13-Dec-17	14-Dec-17	-275	0	[Gantt bars and milestones for BS.SIA_0100]											
BS.SIA_0110	Remedial Works	24	14-Dec-17	15-Jan-18	14-Dec-17	15-Jan-18	-275	106	[Gantt bars and milestones for BS.SIA_0110]											
BS.SIA_0120	EMSD-RB Formal Inspection	1	29-May-18	29-May-18	29-May-18	29-May-18	-381	0	[Gantt bars and milestones for BS.SIA_0120]											
BS.SIA_0130	Remedial Works & Re-Inspection (If Require)	6	30-May-18	05-Jun-18	30-May-18	05-Jun-18	-381	0	[Gantt bars and milestones for BS.SIA_0130]											
BS.SIA_0140	EMSD Letter of "No Objection" Obtained/ Ready to Open	6	06-Jun-18	12-Jun-18	06-Jun-18	12-Jun-18	-381	0	[Gantt bars and milestones for BS.SIA_0140]											
BS.SIA_Comp	Complete & pass all statutory, joint Inspection & handover to Operation Team for the BS	0		12-Jun-18		12-Jun-18	-471	0	[Gantt bars and milestones for BS.SIA_Comp]											
D: WAC Modification Works (Part B Works)																				
WAC Station Modification Works																				
WMW_0010	Install New Telephone Booth and associated works (NTH)	60	06-Mar-17	20-May-17	06-Mar-17	20-May-17	-381	30	[Gantt bars and milestones for WMW_0010]											
WMW_0020	Relocate 4 Advertising Panels (NTH)	21	27-Jun-17	21-Jul-17	27-Jun-17	21-Jul-17	-392	0	[Gantt bars and milestones for WMW_0020]											
WMW_0030	Finishing, Remedial works & site cleaning	24	13-Nov-17	09-Dec-17	13-Nov-17	09-Dec-17	-381	0	[Gantt bars and milestones for WMW_0030]											
AFC Audit Room																				
INF.AFCp	Interface Access for AFC, C&C DC in new AFC Audit Room inside WAC, Concourse Level	0		28-Dec-15 A		27-Feb-16			[Gantt bars and milestones for INF.AFCp]											
WMW.AFC_0010	Preparation works for works in WAC station	10	28-Dec-15 A	02-Jan-16 A	10-Oct-15	22-Oct-15			[Gantt bars and milestones for WMW.AFC_0010]											
WMW.AFC_0020	Internal Hoarding in WAC station (NTH)	12	04-Jan-16 A	09-Jan-16 A	30-Nov-15	12-Dec-15			[Gantt bars and milestones for WMW.AFC_0020]											
WMW.AFC_0030	Construct new AFC/Audit Room next to Entrance B1, B2, ABWF & BS Works (NTH)	60	28-Dec-15 A	30-Jun-16 A	01-Feb-16	18-Apr-16			[Gantt bars and milestones for WMW.AFC_0030]											



Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)

Progress vs Program (Updated Ending Oct'16)



Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Total Float	Free Float	Gantt Chart											
									2014	2015			2016			2017			2018	
Existing AFC Adult Room, Maxim's & Circle K Kiosks																				
WMW.K_0010	Liaison with MTR/ relevance parties for modification works of existing Kiosks & Audit Roo	36	27-Apr-15 A	30-Jun-15 A	05-Jul-16	15-Aug-16			[Gantt bars for WMW.K_0010]											
WMW.K_0020	Internal Hoarding in WAC station (NTH)	12	31-Oct-16	12-Nov-16	31-Oct-16	12-Nov-16	-411	0	[Gantt bars for WMW.K_0020]											
WMW.K_0030	Modification Works to existing AFC/Audit, Store & Kiosk 3 & 5 (NTH)	90	14-Nov-16	04-Mar-17	14-Nov-16	04-Mar-17	-411	0	[Gantt bars for WMW.K_0030]											
WMW.K_0040	Modification to existing Kiosk 2 (NTH)	90	06-Mar-17	26-Jun-17	06-Mar-17	26-Jun-17	-411	0	[Gantt bars for WMW.K_0040]											
ABWF Works & Misc Works																				
WMW.ABWF_0010	ABWF - Plaster & tiling 29 m2, baffling ceiling 10 m2, metal cladding 9 m2	70	27-Jun-17	16-Sep-17	27-Jun-17	16-Sep-17	-411	0	[Gantt bars for WMW.ABWF_0010]											
Breaking Out WAC Station																				
WMW.BO_0010	Installation protection measurement for break through	2	17-Oct-16 A	19-Oct-16 A	22-Jul-17	24-Jul-17			[Gantt bars for WMW.BO_0010]											
WMW.BO_0020	Breaking out WAC Station - Form opening, core holes & wire cut, 60 no. x 0.9m x 0.9m	54	19-Oct-16 A	20-Oct-17	18-Sep-17	22-Nov-17	-381	0	[Gantt bars for WMW.BO_0020]											
WMW.BO_0030	Breaking out WAC Station - Installation of temporary steel propping	30	23-Sep-17 A	06-Oct-17	23-Sep-17	31-Oct-17	-369	12	[Gantt bars for WMW.BO_0030]											
WMW.BO_0040	Breaking out WAC Station - Construct the portal frame	12	21-Oct-17	04-Nov-17	21-Oct-17	04-Nov-17	-381	0	[Gantt bars for WMW.BO_0040]											
WMW.BO_0050	Demolish the propping steel members	6	06-Nov-17	11-Nov-17	06-Nov-17	11-Nov-17	-381	0	[Gantt bars for WMW.BO_0050]											
Testing and Commissioning																				
WMW.C_0010	Testing and Commissioning	30	22-Jul-17	25-Aug-17	22-Jul-17	25-Aug-17	-392	19	[Gantt bars for WMW.C_0010]											
WMW.K_Comp	Specified Part 2B - Complete all works at the 2 new Shop Kiosks and hand over to the E	0		16-Sep-17		16-Sep-17	-503	0	[Gantt bars for WMW.K_Comp]											
E. WAC Station Improvement Works (Part C Works)																				
Improvement Works to WAC Station																				
WIW_0010	Modify, provide & install new glass barrier to suit new AFC gates (NTH)	34	12-Oct-15 A	20-Nov-15 A	01-Nov-16	09-Dec-16			[Gantt bars for WIW_0010]											
WIW_0020	Provide and install additional AFC gates (NTH)	34	06-Mar-17	18-Apr-17	06-Mar-17	18-Apr-17	-40	0	[Gantt bars for WIW_0020]											
WIW_0030	Provide builder works for TIMS relocation (NTH)	40	11-Dec-17	29-Jan-18	11-Dec-17	29-Jan-18	-381	0	[Gantt bars for WIW_0030]											
WIW_0040	T&C by Designated Contractor for TIMS (NTH)	40	30-Jan-18	20-Mar-18	30-Jan-18	20-Mar-18	-381	0	[Gantt bars for WIW_0040]											
WIW_0050	Make Good builder works for TIMS (NTH)	53	21-Mar-18	28-May-18	21-Mar-18	28-May-18	-381	0	[Gantt bars for WIW_0050]											
WIW_Comp	E3- All works in milestone E completed - Programmed	0		28-May-18		28-May-18	-472	0	[Gantt bars for WIW_Comp]											

- Actual Level of Effort
- Critical Remaining ...
- Primary Baseline
- Actual Work
- Remaining Work
- ◆ Baseline Milestone
- ◆ Milestone

**Contract C6593-13C Wan Chai Station Lee Tung Street Subway
Master Program (Rev.C)**


Progress vs Program (Updated Ending Oct'16)



Appendix C

Monitoring Locations

Ca:\Programs\Bentley\MicroStation\18\SELECTseries\WorkSpace\System\trcg\WTR_PDF_BM_COA_3000P.dwg
 04/2024/5/REP/REP1/CONTR/CSS/556/NE/18/0_2/4_005/05P
 PLOT BY: MTR
 FILE NAME: 18/04/2024

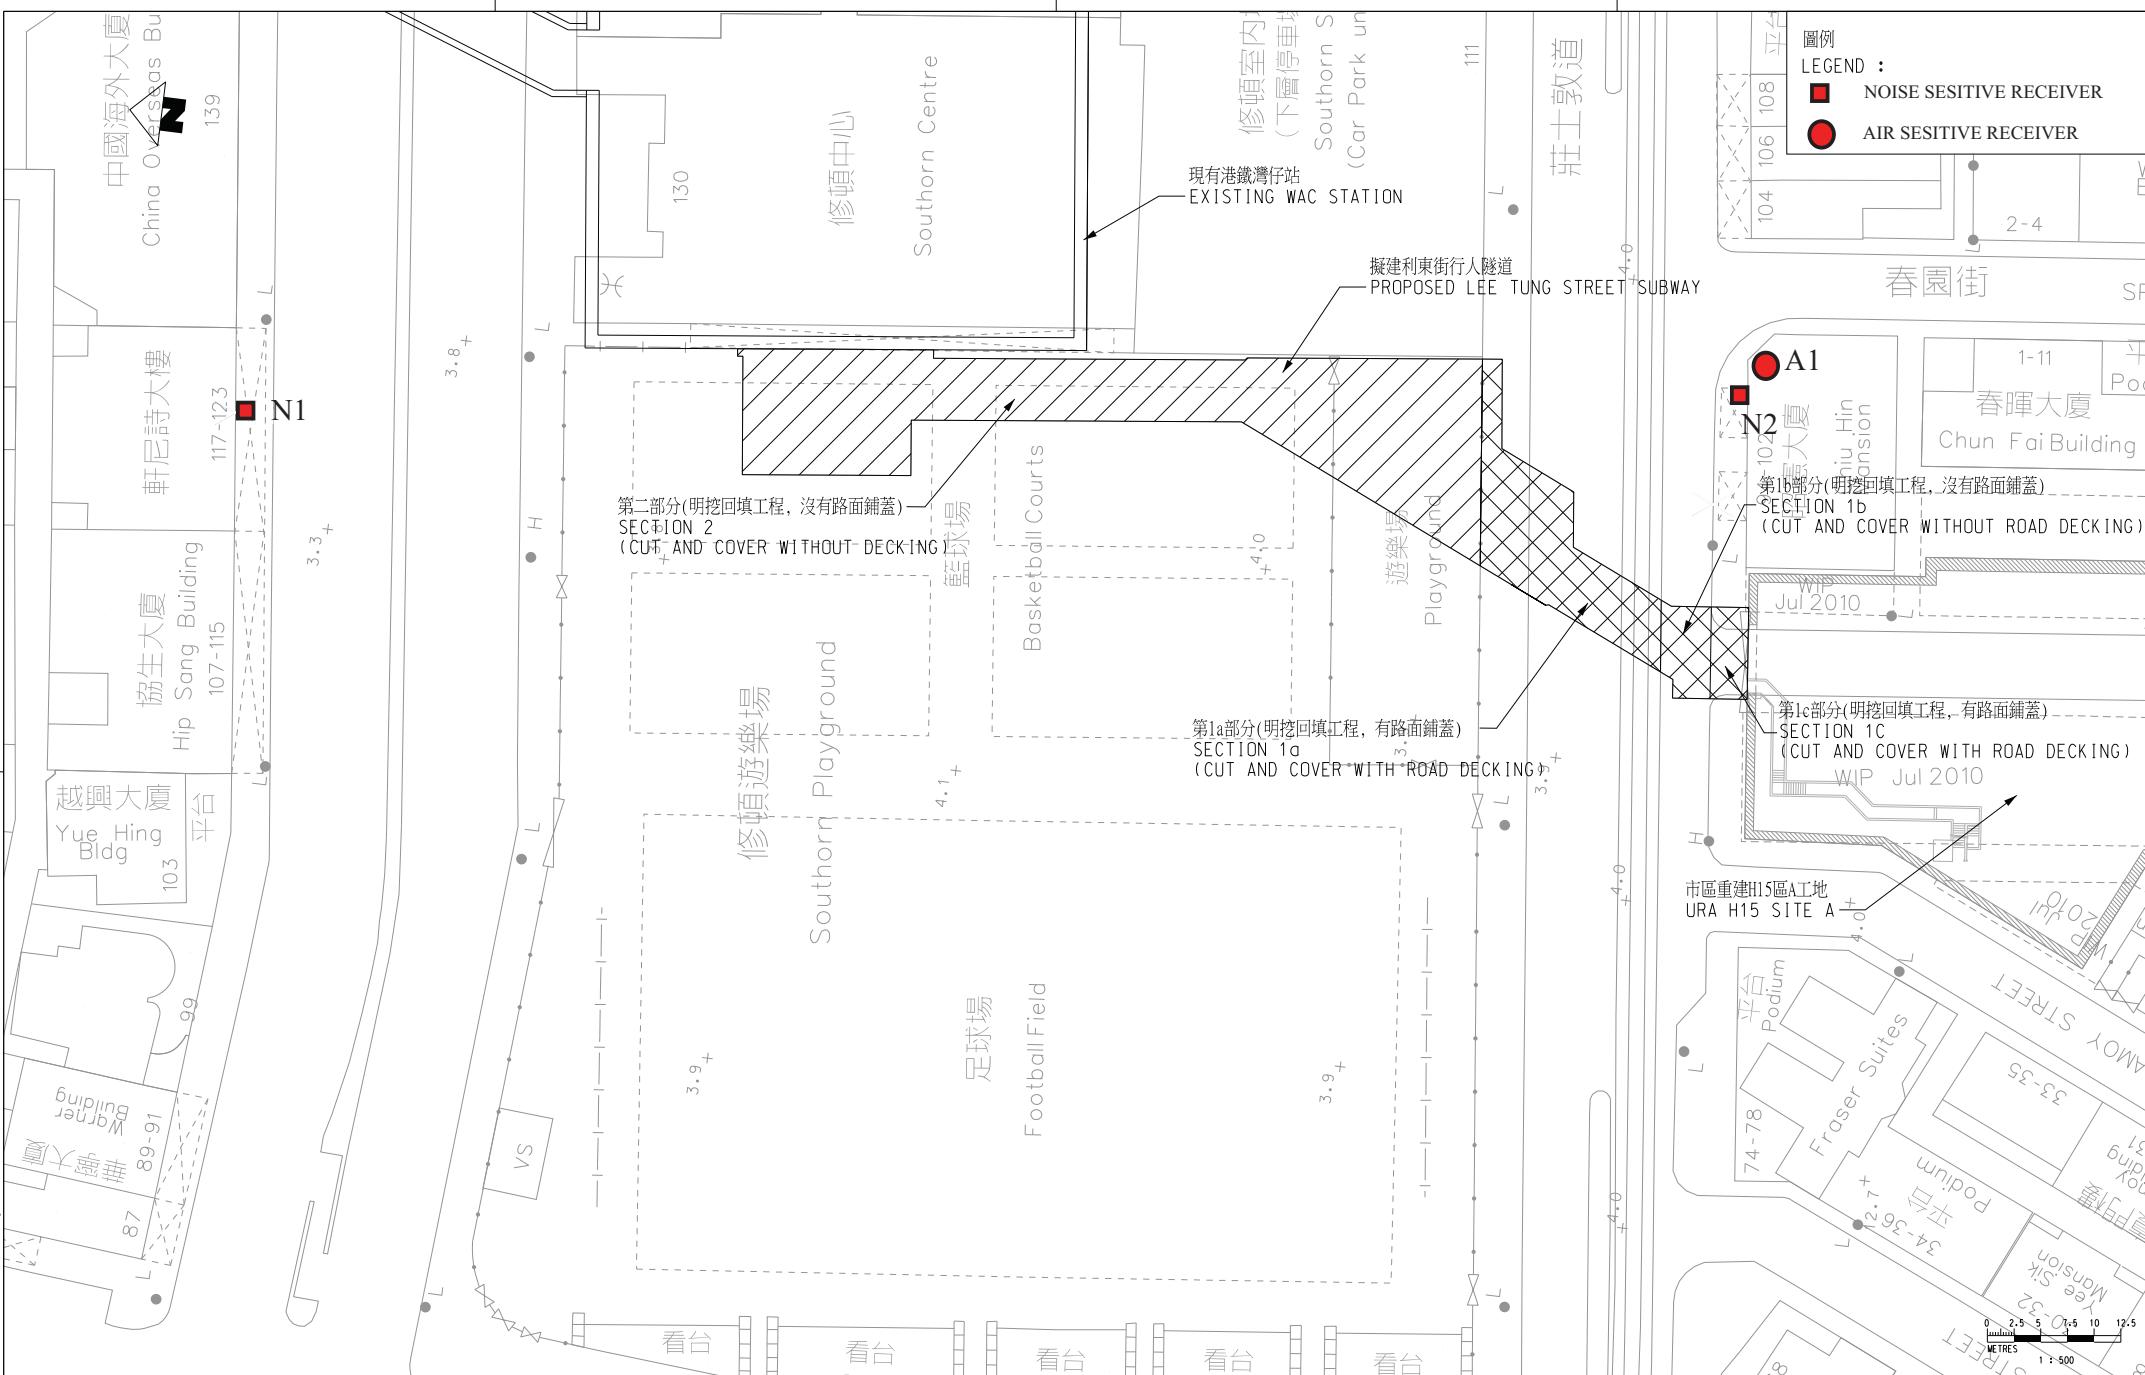

圖例
LEGEND :

- NOISE SENSITIVE RECEIVER
- AIR SENSITIVE RECEIVER

TITLE
 CONSULTANCY AGREEMENT NO. NEX/1050
 DETAILED DESIGN FOR LEE TUNG STREET SUBWAY
 LOCATION OF NOISE AND AIR SENSITIVE RECEIVER

SCALE
 1:500 (A3)

DRAWING NO.

REV.

MTR

WAC STATION LEE TUNG STREET SUBWAY

ORIGINATOR

Mott MacDonald

25F Two Landmark East
 100 Tsim Sha Tsui Street
 Kowloon, Hong Kong
 Tel: +852 2511 8888
 www.mottmacdonald.com.hk

CADD REF.

REV	DESCRIPTION	BY	DATE	APPROVED	REV	DESCRIPTION	BY	DATE	APPROVED
D	GENERAL REVISION								
C	GENERAL REVISION								
B	GENERAL REVISION								
A	PROJECT PROFILE								

DRAWN

DESIGNED

CHECKED

APPROVED

DATE

DO NOT SCALE DRAWINGS. ALL DIMENSIONS SHALL BE VERIFIED ON SITE.
 MOTT MACDONALD CORPORATION LIMITED 2008 COPYRIGHT IN RESPECT OF THIS DRAWING. A DOCUMENT IS MADE BY THE MOTT MACDONALD CORPORATION LIMITED AT HONG KONG. NO REPRESENTATION IS MADE BY THIS DOCUMENT OR ANY PART THEREOF IN RESPECT OF THE ACCURACY OF THE INFORMATION CONTAINED HEREIN. THE USER SHALL BE RESPONSIBLE FOR THE PROPER USE OF THIS DOCUMENT AND THE USER SHALL BE RESPONSIBLE FOR THE PROPER USE OF THIS DOCUMENT AND THE USER SHALL BE RESPONSIBLE FOR THE PROPER USE OF THIS DOCUMENT.

Appendix D

**Calibration Certificate of
Monitoring Equipment**

Location : Chiu Hin Mansion
 Location ID : A1

Date of Calibration: 13-Oct-16
 Next Calibration Date: 13-Dec-16
 Technician: Mr. Ip Ka Hing

CONDITIONS

Sea Level Pressure (hPa)	<input type="text" value="1013.5"/>	Corrected Pressure (mm Hg)	<input type="text" value="760.125"/>
Temperature (°C)	<input type="text" value="26.0"/>	Temperature (K)	<input type="text" value="299"/>

CALIBRATION ORIFICE

Make->	<input type="text" value="TISCH"/>	Qstd Slope ->	<input type="text" value="2.00411"/>
Model->	<input type="text" value="5025A"/>	Qstd Intercept ->	<input type="text" value="-0.03059"/>
Serial # ->	<input type="text" value="1612"/>		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.3	5.3	10.6	1.637	51	50.83	Slope = 38.9659 Intercept = -11.8329 Corr. coeff. = 0.9961
13	4	4	8	1.424	45	44.85	
10	3.1	3.1	6.2	1.256	38	37.88	
7	2.5	2.5	5	1.129	32	31.90	
5	1.6	1.6	3.2	0.906	23	22.92	

Calculations :


$Q_{std} = 1/m[\sqrt{H_2O(P_a/P_{std})(T_{std}/T_a)} - b]$
 $IC = I[\sqrt{P_a/P_{std}}(T_{std}/T_a)]$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$1/m((I)[\sqrt{298/T_{av}}(P_{av}/760)] - b)$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

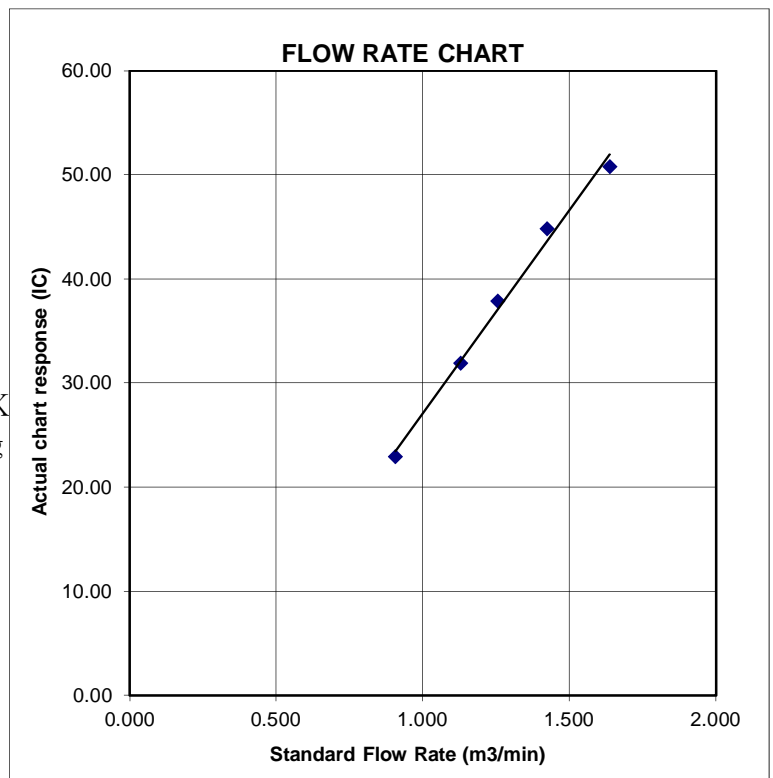

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Mar 14, 2016 Rootsmeter S/N 0438320 Ta (K) - 295
 Operator Tisch Orifice I.D. - 1612 Pa (mm) - 745.49

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.3770	3.2	2.00
2	NA	NA	1.00	0.9710	6.4	4.00
3	NA	NA	1.00	0.8710	7.8	5.00
4	NA	NA	1.00	0.8310	8.7	5.50
5	NA	NA	1.00	0.6860	12.6	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9866	0.7165	1.4078	0.9957	0.7231	0.8896
0.9824	1.0117	1.9909	0.9914	1.0210	1.2581
0.9804	1.1256	2.2259	0.9894	1.1360	1.4066
0.9793	1.1785	2.3345	0.9883	1.1893	1.4753
0.9741	1.4200	2.8155	0.9830	1.4330	1.7792
Qstd slope (m) = 2.00411			Qa slope (m) = 1.25494		
intercept (b) = -0.03059			intercept (b) = -0.01933		
coefficient (r) = 0.99995			coefficient (r) = 0.99995		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)
 Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
 Qa = Va/Time

For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b}
 Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b}



Certificate of Calibration 校正證書

Certificate No. : C164098
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC16-0843) Date of Receipt / 收件日期 : 15 July 2016
Description / 儀器名稱 : Sound Level Calibrator (EQ085)
Manufacturer / 製造商 : Rion
Model No. / 型號 : NC-73
Serial No. / 編號 : 10655561
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C Relative Humidity / 相對濕度 : (55 ± 20)%
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration


DATE OF TEST / 測試日期 : 27 July 2016


TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification & user's specified acceptance criteria. (after adjustment)
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By : 
測試 : _____
H T Wong
Technical Officer

Certified By : 
核證 : _____
K C Lee
Project Engineer

Date of Issue : 28 July 2016
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C164098
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C163709
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C161175

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

5.1.1 Before Adjustment

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	* 93.4	± 0.5	± 0.2

* Out of Mfr's Spec.

5.1.2 After Adjustment

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.5	± 0.2

5.2 Frequency Accuracy

5.2.1 Before Adjustment

UUT Nominal Value (kHz)	Measured Value (kHz)	User's Spec.	Uncertainty of Measured Value (Hz)
1	0.955	1 kHz ± 6 %	± 1

5.2.2 After Adjustment

UUT Nominal Value (kHz)	Measured Value (kHz)	User's Spec.	Uncertainty of Measured Value (Hz)
1	0.954	1 kHz ± 6 %	± 1

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。



Certificate of Calibration

校正證書

Certificate No. : C164098
證書編號

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com



Certificate of Calibration 校正證書

Certificate No. : C162125
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC16-0843) Date of Receipt / 收件日期 : 14 April 2016
Description / 儀器名稱 : Acoustical Calibrator (EQ082)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 4231
Serial No. / 編號 : 2713428
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$ Relative Humidity / 相對濕度 : $(55 \pm 20)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 22 April 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By : 
測試 : _____
H T Wong
Technical Officer

Certified By : 
核證 : _____
K C Lee
Project Engineer

Date of Issue : 25 April 2016
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C162125
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C153519
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C161175

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.1		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

Certificate of Calibration

校正證書

Certificate No. : C161796

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC16-0662)

Date of Receipt / 收件日期 : 22 March 2016

Description / 儀器名稱 : Sound Level Meter (EQ015)

Manufacturer / 製造商 : Rion

Model No. / 型號 : NL-52

Serial No. / 編號 : 00142581

Supplied By / 委託者 : Action-United Environmental Services and Consulting

Unit A, 20/F., Gold King Industrial Building,

35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$

Relative Humidity / 相對濕度 : $(55 \pm 20)\%$

Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 6 April 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By

測試

:

H T Wong

Technical Officer

Certified By

核證

:

K/C Lee

Project Engineer

Date of Issue

簽發日期

:

7 April 2016

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C161796
證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL280	40 MHz Arbitrary Waveform Generator	C160077
CL281	Multifunction Acoustic Calibrator	PA160023

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.4	± 1.1

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
30 - 130	L _A	A	Fast	94.00	1	94.4 (Ref.)
				104.00		104.4
				114.00		114.4

IEC 61672 Class 1 Spec. : ± 0.6 dB per 10 dB step and ± 1.1 dB for overall different.

- 6.2 Time Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
30 - 130	L _A	A	Fast	94.00	1	94.4	Ref.
			Slow			94.4	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 – 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606

Fax/傳真: 2744 8986

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com

Certificate of Calibration

校正證書

Certificate No. : C161796
證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _A	A	Fast	94.00	63 Hz	68.1	-26.2 ± 1.5
					125 Hz	78.2	-16.1 ± 1.5
					250 Hz	85.7	-8.6 ± 1.4
					500 Hz	91.1	-3.2 ± 1.4
					1 kHz	94.4	Ref.
					2 kHz	95.6	+1.2 ± 1.6
					4 kHz	95.4	+1.0 ± 1.6
					8 kHz	93.3	-1.1 (+2.1 ; -3.1)
					12.5 kHz	89.9	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 61672 Class 1 Spec. (dB)
Range (dB)	Function	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
30 - 130	L _C	C	Fast	94.00	63 Hz	93.5	-0.8 ± 1.5
					125 Hz	94.2	-0.2 ± 1.5
					250 Hz	94.3	0.0 ± 1.4
					500 Hz	94.4	0.0 ± 1.4
					1 kHz	94.4	Ref.
					2 kHz	94.2	-0.2 ± 1.6
					4 kHz	93.6	-0.8 ± 1.6
					8 kHz	91.4	-3.0 (+2.1 ; -3.1)
					12.5 kHz	88.0	-6.2 (+3.0 ; -6.0)

Remarks : - UUT Microphone Model No. : UC-59 & S/N : 06015

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value :

94 dB : 63 Hz - 125 Hz	: ± 0.35 dB
250 Hz - 500 Hz	: ± 0.30 dB
1 kHz	: ± 0.20 dB
2 kHz - 4 kHz	: ± 0.35 dB
8 kHz	: ± 0.45 dB
12.5 kHz	: ± 0.70 dB
104 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Certificate of Calibration

校正證書

Certificate No. : C162177
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC16-0843) Date of Receipt / 收件日期 : 14 April 2016

Description / 儀器名稱 : Integrating Sound Level Meter (EQ006)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 2238
Serial No. / 編號 : 2285762
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : (23 ± 2)°C Relative Humidity / 相對濕度 : (55 ± 20)%
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 25 April 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
The results do not exceed manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Fluke Everett Service Center, USA
- Rohde & Schwarz Laboratory, Germany

Tested By : 
測試 : _____
H T Wong
Technical Officer

Certified By : 
核證 : _____
K C Lee
Project Engineer

Date of Issue : 27 April 2016
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C162177
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- Self-calibration using laboratory acoustic calibrator was performed before the test from 6.1.1.2 to 6.4.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C160077
CL281	Multifunction Acoustic Calibrator	PA160023

- Test procedure : MA101N.

- Results :

6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

6.1.1.1 Before Self-calibration

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
50 - 130	L _{AFP}	A	F	94.00	1	94.2

6.1.1.2 After Self-calibration

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L _{AFP}	A	F	94.00	1	94.0	± 0.7

6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
50 - 130	L _{AFP}	A	F	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		113.9

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C162177
證書編號

6.2 Time Weighting

6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L _{AFP}	A	F	94.00	1	94.0	Ref.
	L _{ASP}		S			94.0	± 0.1
	L _{AIP}		I			94.1	± 0.1

6.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
30 - 110	L _{AFP}	A	F	106.0	Continuous	106.0	Ref.
	L _{AFMax}				200 ms	105.0	-1.0 ± 1.0
	L _{ASP}		S		Continuous	106.0	Ref.
	L _{ASMax}				500 ms	102.0	-4.1 ± 1.0

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{AFP}	A	F	94.00	31.5 Hz	55.1	-39.4 ± 1.5
					63 Hz	67.9	-26.2 ± 1.5
					125 Hz	77.9	-16.1 ± 1.0
					250 Hz	85.3	-8.6 ± 1.0
					500 Hz	90.7	-3.2 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	95.2	+1.2 ± 1.0
					4 kHz	95.0	+1.0 ± 1.0
					8 kHz	91.0	-1.1 (+1.5 ; -3.0)
					12.5 kHz	89.8	-4.3 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C162177

證書編號

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{CFP}	C	F	94.00	31.5 Hz	91.5	-3.0 ± 1.5
					63 Hz	93.4	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.0
					250 Hz	94.1	0.0 ± 1.0
					500 Hz	94.1	0.0 ± 1.0
					1 kHz	94.1	Ref.
					2 kHz	93.9	-0.2 ± 1.0
					4 kHz	93.2	-0.8 ± 1.0
					8 kHz	92.9	-3.0 (+1.5 ; -3.0)
					12.5 kHz	87.9	-6.2 (+3.0 ; -6.0)

6.4 Time Averaging

UUT Setting				Applied Value					UUT Reading (dB)	IEC 60804 Type 1 Spec. (dB)	
Range (dB)	Parameter	Frequency Weighting	Integrating Time	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)			
30 - 110	L _{Aeq}	A	10 sec.	4	1	1/10	110.0	100	100.0	± 0.5	
								1/10 ²	90	89.9	± 0.5
								1/10 ³	80	79.2	± 1.0
								1/10 ⁴	70	69.2	± 1.0
			60 sec.								
			5 min.								

Remarks : - UUT Microphone Model No. : 4188 & S/N : 2812705

- Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

94 dB	31.5 Hz - 125 Hz	: ± 0.35 dB
	250 Hz - 500 Hz	: ± 0.30 dB
	1 kHz	: ± 0.20 dB
	2 kHz - 4 kHz	: ± 0.35 dB
	8 kHz	: ± 0.45 dB
	12.5 kHz	: ± 0.70 dB
104 dB	1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB	1 kHz	: ± 0.10 dB (Ref. 94 dB)
Burst equivalent level		: ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Appendix E

HOKLAS-Accreditation Certificate of the Testing Laboratory



Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong
香港新界葵涌永業街1-3號忠信針織中心11樓

has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a
為香港認可處執行機關根據認可諮詢委員會建議而接受的

HOKLAS Accredited Laboratory
「香港實驗所認可計劃」認可實驗所

This laboratory meets the requirements of ISO / IEC 17025 : 2005 – General requirements for the competence of testing and calibration laboratories and it has been accredited for performing specific tests or calibrations as listed in the HOKLAS Directory of Accredited Laboratories within the test category of
此實驗所符合ISO / IEC 17025 : 2005 – 《測試及校正實驗所能力的通用規定》所訂的要求，獲認可進行載於香港實驗所認可計劃《認可實驗所名冊》內下述測試類別中的指定
測試或校正工作

Environmental Testing
環境測試

This laboratory is accredited in accordance with the recognised International Standard ISO / IEC 17025 : 2005.
本實驗所乃根據公認的國際標準 ISO / IEC 17025 : 2005 獲得認可。

This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (see joint IAF-ILAC-ISO Communiqué).
這項認可資格演示在指定範疇所需的技術能力及實驗所質量管理體系的運作
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive
香港認可處根據認可處執行機關的權限在此蓋上通用印章

CHAN Sing Sing, Terence, Executive Administrator
執行幹事 陳成城
Issue Date : 5 May 2009
簽發日期：二零零九年五月五日

Registration Number : **HOKLAS 066**
註冊號碼：

Date of First Registration : 15 September 1995
首次註冊日期：一九九五年九月十五日



Appendix F

Event and Action Plan

Event and Action Plan for Construction Noise

Event	Action			
	ET	IEC	ER	Contractor
Action Level	1. Notify IEC and Contractor. 2. Carry out investigation. 3. Report the results of investigation to the IEC and Contractor. 4. Discuss with the Contractor and formulate remedial measures 5. Increase monitoring frequency to check mitigation effectiveness.	1. Review the analyzed result submitted by ET. 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly. 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of exceedance 2. Notify Contractor 3. Require Contractor to propose remedial measures for the analyzed noise problem 4. Ensure remedial measures are properly implemented.	1. Submit noise mitigation proposals to IEC 2. Implement noise mitigation proposals
Limit Level	1. Notify IEC, ER, EPD and Contractor, and follow other actions 2. Identify source 3. Repeat measurement to confirm findings 4. Increase monitoring frequency 5. Check Contractor's working procedures to determine possible mitigation to be implemented 6. Inform IEC, ER and EPD the causes and actions taken for the exceedances 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD, ER informed of the results 8. If exceedance stops, cease additional monitoring	1. Discuss amongst ER, ET and Contractor on the potential remedial actions 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ET accordingly 3. Supervise the implementation of remedial measures	1. Confirm receipt of notification of exceedances 2. Notify Contractor 3. Require Contractor to propose remedial measures 4. Ensure remedial measures are properly implemented 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance 2. Submit proposals for remedial actions to IEC within 3 working days of notifications 3. Implement the agreed proposals 4. Revise and resubmit proposals if problem still not under control 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated

Event and Action Plan for Air Quality

Event	Action			
	ET	IEC	ER	Contractor
Action Level				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source; 2. If valid, inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and EPD; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency to daily; 5. Discuss with IEC and Contractor on remedial action required; 6. If exceedance continues, arrange meeting with IEC and ER; 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervisor implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial Measure properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial action to IEC within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
Limit Level				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source; 2. Inform ER and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and the Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IEC, ER, Contractor and EPD; 2. Identify sources; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ET accordingly. 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Appendix G

Monitoring Schedule

Monitoring Schedule in the Reporting Period – November 2016

DATE		AIR QUALITY	NOISE
		24-HOUR TSP	L _{EQ} 30MIN
TUE	1-Nov-16		
WED	2-Nov-16		
THU	3-Nov-16		✓
FRI	4-Nov-16	✓	
SAT	5-Nov-16		
SUN	6-Nov-16		
MON	7-Nov-16		
TUE	8-Nov-16		
WED	9-Nov-16		
THU	10-Nov-16	✓	
FRI	11-Nov-16		✓
SAT	12-Nov-16		
SUN	13-Nov-16		
MON	14-Nov-16		
TUE	15-Nov-16		
WED	16-Nov-16	✓	
THU	17-Nov-16		✓
FRI	18-Nov-16		
SAT	19-Nov-16		
SUN	20-Nov-16		
MON	21-Nov-16		
TUE	22-Nov-16	✓	
WED	23-Nov-16		
THU	24-Nov-16		✓
FRI	25-Nov-16		
SAT	26-Nov-16		
SUN	27-Nov-16		
MON	28-Nov-16	✓	
TUE	29-Nov-16		✓
WED	30-Nov-16		

✓	Monitoring Day
	Sunday or Public Holiday

Air Quality Monitoring Location

A1 - balcony at 1/F of Chiu Hin Mansion

Construction Noise Monitoring Location:

N1 - 2/F floor of Hennessey Building

N2 - balcony at 1/F of Chiu Hin Mansion

Monitoring Schedule for the Coming Month – December 2016

DATE		AIR QUALITY	NOISE
		24-HOUR TSP	L _{EQ} 30MIN
THU	1-DEC-16		
FRI	2-DEC-16		
SAT	3-DEC-16	✓	
SUN	4-DEC-16		
MON	5-DEC-16		
TUE	6-DEC-16		
WED	7-DEC-16		
THU	8-DEC-16		✓
FRI	9-DEC-16	✓	
SAT	10-DEC-16		
SUN	11-DEC-16		
MON	12-DEC-16		
TUE	13-DEC-16		
WED	14-DEC-16		
THU	15-DEC-16	✓	✓
FRI	16-DEC-16		
SAT	17-DEC-16		
SUN	18-DEC-16		
MON	19-DEC-16		
TUE	20-DEC-16		
WED	21-DEC-16	✓	✓
THU	22-DEC-16		
FRI	23-DEC-16		
SAT	24-DEC-16	✓	
SUN	25-DEC-16		
MON	26-DEC-16		
TUE	27-DEC-16		
WED	28-DEC-16		
THU	29-DEC-16		✓
FRI	30-DEC-16	✓	
SAT	31-DEC-16		

✓	Monitoring Day
	Sunday or Public Holiday

Remarks:

Designated Location for Impact noise measurement:

- N1 Hennessey Building; and
- N2 Chiu Hin Mansion

Designated Location for Impact air quality monitoring

- A1 Chiu Hin Mansion

Appendix H

Database of Monitoring Results


Result of 24-hour TSP Monitoring

Location: A1 (balcony at 1/F of Chiu Hin Mansion)															
Date	Sample Number	Elapsed Time			Chart Reading			Ave. Temp. (°C)	Standard			Filter Weight (g)		Weight Dust Collected (g)	Dust 24-hour TSP in Air (µg/m ³)
		Initial	Final	Actual (min)	Min	Max	Ave		Ave. Press. (hPa)	Flow Rate (m ³ /min)	Air Volume (std m ³)	Initial	Final		
4-Nov-16	20126	18614.98	18639.08	1446.00	41	41	41.0	22.4	1015.2	1.36	1969	2.8882	3.0497	0.1615	82
10-Nov-16	20150	18639.08	18663.19	1446.60	41	41	41.0	17.7	1020.1	1.37	1986	2.8746	2.9888	0.1142	58
16-Nov-16	20227	18663.19	18687.28	1445.40	40	43	41.5	21.7	1017.8	1.38	1990	2.8186	2.9814	0.1628	82
22-Nov-16	20226	18687.28	18710.85	1414.20	40	40	40.0	22.7	1013.3	1.33	1887	2.8142	2.8812	0.0670	36
28-Nov-16	20240	18710.85	18734.96	1446.60	40	40	40.0	18.1	1020.9	1.35	1947	2.8383	2.9759	0.1376	71



Appendix I

Graphical Plots

Air Quality

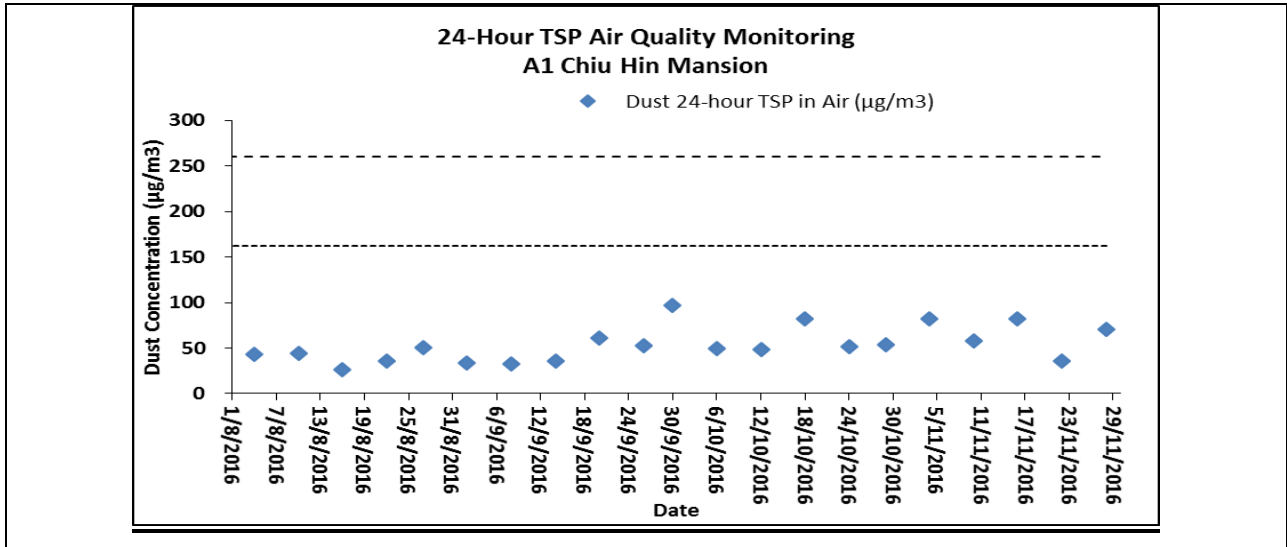

Construction Noise

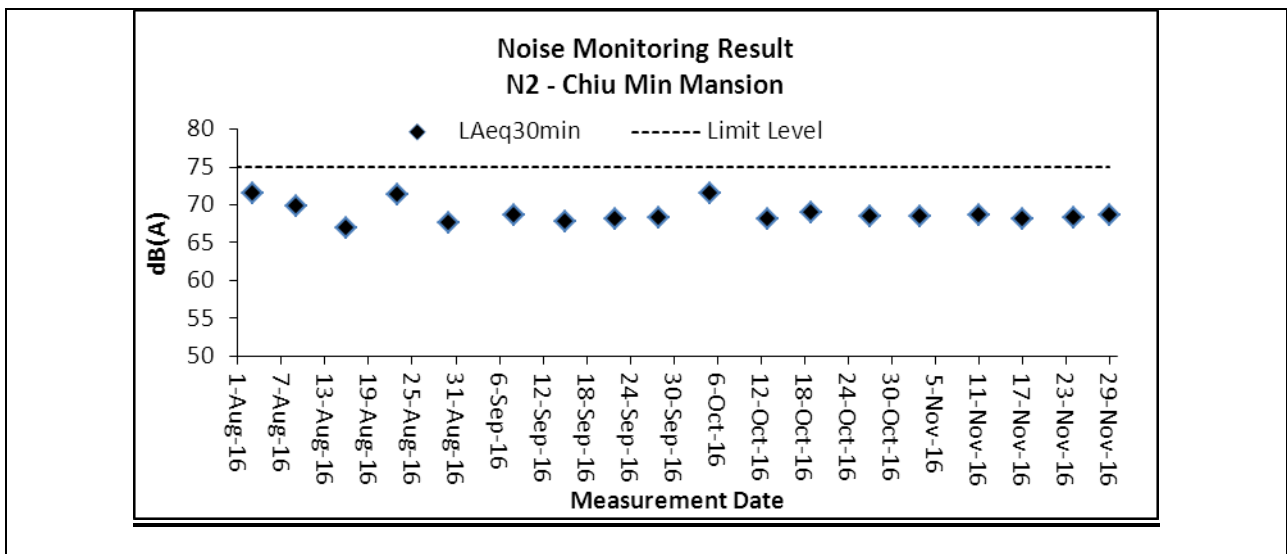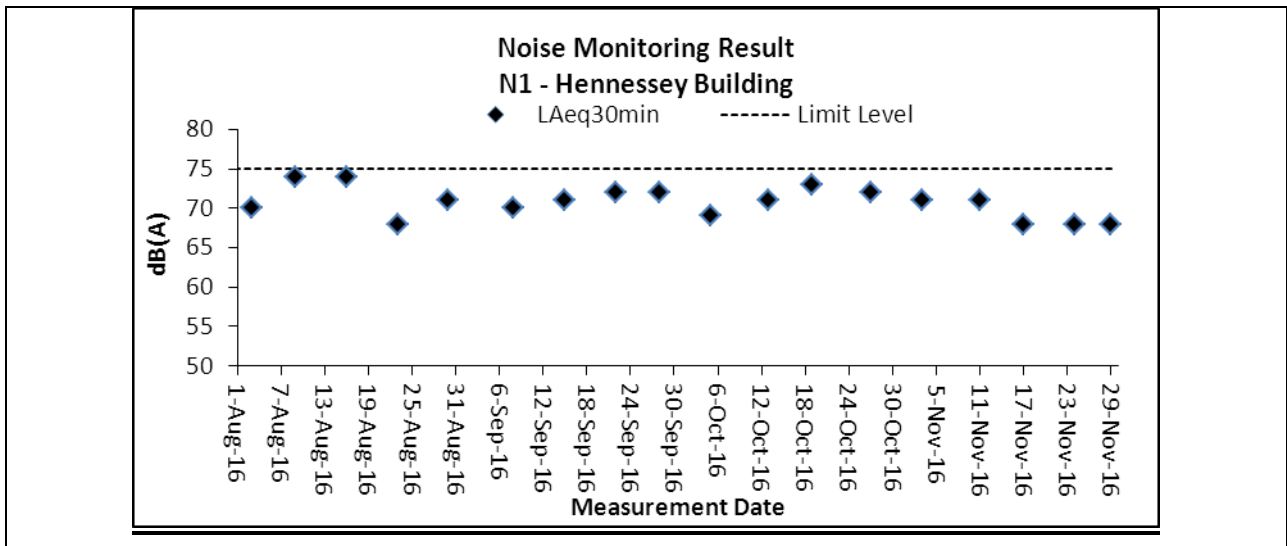

Appendix J

Meteorological Information

Meteorological Data downloaded from HKO in the Reporting Period							
Date	Weather	Total Rainfall (mm)	Kings Park Station				
			Mean Air Temp. (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction	
1-Nov-16	Tue	Moderate easterly winds, becoming fresh northerlies later tomorrow.	0	23.3	11.5	66	NE
2-Nov-16	Wed	It will be cool. Cloudy to overcast with a few rain patches.	0	22.4	9.8	65	N/NE
3-Nov-16	Thu	Sunny intervals in the afternoon. Light winds. Winds will strengthen	0	21.9	9	59	N/NE
4-Nov-16	Fri	It will be cool. Cloudy to overcast with a few rain patches.	0	22.2	6.5	61.7	N/NE
5-Nov-16	Sat	Moderate easterly winds, becoming fresh northerlies later tomorrow.	0	23.8	8.6	75.8	N/NE
6-Nov-16	Sun	Sunny intervals in the afternoon. Light winds. Winds will strengthen	0	24.2	6.1	75	E/SE
7-Nov-16	Mon	Moderate easterly winds, becoming fresh northerlies later tomorrow.	0	25.3	8	76.2	E/NE
8-Nov-16	Tue	Sunny intervals in the afternoon. Light winds. Winds will strengthen	4.8	24.6	6.9	79	E/SE
9-Nov-16	Wed	It will be cool. Cloudy to overcast with a few rain patches.	1.3	19.6	7.5	78	NE
10-Nov-16	Thu	It will be cool. Cloudy to overcast with a few rain patches.	1.9	16.8	6.9	80.5	NE
11-Nov-16	Fri	Sunny intervals in the afternoon. Light winds. Winds will strengthen	Trace	19.4	6.1	77.2	N/NE
12-Nov-16	Sat	It will be cool. Cloudy to overcast with a few rain patches.	0.2	23.7	7.5	82.5	N/NE
13-Nov-16	Sun	It will be cool. Cloudy to overcast with a few rain patches.	0	25.1	5.5	83.5	E/SE
14-Nov-16	Mon	Moderate easterly winds, becoming fresh northerlies later tomorrow.	0	25.4	5.5	81	E/SE
15-Nov-16	Tue	Moderate easterly winds, becoming fresh northerlies later tomorrow.	Trace	26.3	8.2	77.2	E/SE
16-Nov-16	Wed	Mainly cloudy. Sunny periods in the afternoon. Moderate to fresh easterly winds	Trace	24.5	11.2	77.2	E/SE
17-Nov-16	Thu	Mainly fine. Moderate easterly winds, occasionally fresh offshore.	Trace	25.7	6.6	73	E/SE
18-Nov-16	Fri	It will be cool. Cloudy to overcast with a few rain patches.	Trace	25	8	79.5	E/SE
19-Nov-16	Sat	It will be cool. Cloudy to overcast with a few rain patches.	1.4	26	9.2	78.9	SE
20-Nov-16	Sun	It will be cool. Cloudy to overcast with a few rain patches.	Trace	25.6	15	78	SE
21-Nov-16	Mon	Mainly cloudy. Moderate easterly winds, occasionally fresh offshore.	0.3	24.2	11.8	87.5	E/SE
22-Nov-16	Tue	Cloudy to overcast with occasional rain.	36.5	22.4	12.1	90	E/SE
23-Nov-16	Wed	Cloudy to overcast with occasional rain.	25.9	18.5	8.9	92.5	E/SE
24-Nov-16	Thu	Mainly cloudy with one or two light rain patches.	Trace	17.3	11.2	70	E/SE
25-Nov-16	Fri	Mainly cloudy with one or two light rain patches.	0.1	19.5	9.2	74	N/NE
26-Nov-16	Sat	Mainly fine and dry. Moderate northerly winds, fresh at times.	50.3	16.5	11.2	75.8	N/NE
27-Nov-16	Sun	Cloudy to overcast with occasional rain.	8.6	16	7.5	65	NE
28-Nov-16	Mon	Mainly cloudy with one or two light rain patches.	0	18.3	9.7	62	E/SE
29-Nov-16	Tue	Mainly fine and dry. Moderate northerly winds, fresh at times.	0	18.9	7.5	59	E/NE
30-Nov-16	Wed	Mainly fine and dry. Moderate northerly winds, fresh at times.	0	19.9	9.2	59.5	N/NE

Appendix K

Monthly Summary Waste Flow Table

Wan Chai Station Lee Tung Street Subway- C6593-13C

Monthly Summary Waste Flow Table for 2016

Name of Employer: MTR Corporation Limited															Contract No.: C65931-13C					
Month	Actual Quantities of Inert C&D Materials Generated Monthly										Actual Quantities of Non-Inert C&D Wastes Generated Monthly					Actual Quantities of Non-Inert C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete	Building Debris	Mixed Rock & Soil	Bentonite	Rubbish	Slurry	Rock	Soil	Reused in this Project	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse	Metals	Paper/ cardboard packaging	Plastics	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in ton)	(in ton)	(in ton)	(in Litre)	(in ton)
Jan	0.01559	0	0	0	0	0	0	0	0.01559	0	0	0	0	0.001	0	0	0	0	0	0
Feb	0.007	0	0	0	0	0	0	0	0	0	0	0	0	0.007	0	0	0	0	0	0
Mar	0.03685	0	0	0	0	0	0	0	0.03685	0	0	0	0	0.001	0	0	0	0	0	0
Apr	0.03399	0	0	0	0	0	0	0	0.03399	0	0	0	0	0.001	0	0	0	1.2	0	0
May	0.09171	0	0	0	0	0	0	0	0.09171	0	0	0	0	0.001	0	0	0	0	0	0
Jun	0.90981	0	0	0	0	0	0	0	0.90981	0	0	0	0	0.001	0	0	0	0	0	0
Jul	0.36411	0	0	0	0	0	0	0	0.36411	0	0	0	0	0.02	0	0	0	0	0	0
Aug	0.12377	0	0	0	0	0	0	0	0.12377	0	0	0	0	0.001	0	0	0	0	0	0
Sep	0.13455	0	0	0	0	0	0	0	0.13455	0	0	0	0	0.001	0	0	0	0	0	0
Oct	0.26595	0	0	0	0	0	0	0	0.26495	0	0	0	0	0.001	0	0	0	0	0	0
Nov	0.61515	0	0	0	0	0	0	0	0.61515	0	0	0	0	0	0	0	0	0	0	0
Dec	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Total	2.59848	0	0	0	0	0	0	0	2.59048	0	0	0	0	0.035	0	0	0	1.2	0	0

Appendix L

Implementation Schedule for Environmental Mitigation Measures (ISEMM)

Project Profile Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Parties	Location of the measure	When to implement the measure	Relevant requirements or standards for the measure to achieve
NOISE IMPACT						
S.5.1.1	<u>Use of quieter plant</u>	To minimize construction noise emissions	Contractor	Work site	Construction Stage	ProPECC PN2/93 and Noise Control Ordinance
S.5.1.1	<u>Use of noise enclosure and movable barrier</u> <ul style="list-style-type: none"> • movable barrier can achieve a 5 dB(A) reduction for movable PME and 10 dB(A) reduction for stationary PME; • noise enclosure can achieve 15dB(A) reduction for PME; • noise enclosure is proposed to be built after open excavation in order to minimize the noise impact due to further excavation work and construction of subway. The enclosure should either be provided with acoustic door for access purpose which should be kept closed during the construction works or should be designed with no direct line of sight from the open side to the NSRs; • A typical design barrier with a steel frame of vertical / cantilever type would be adopted and located close to the noise generating part of PME; • Barrier material of surface mass in excess of 7kg/m² shall be required to achieve the maximum screening effect (and minimum 10kg/m² for noise enclosure); • The length of barrier should generally be at least five times greater than its height and the minimum height of a barrier should be such that no part of the noise source will be visible from the noise sensitive receiver being protected. 	To minimize construction noise emissions	Contractor	Work site	Construction Stage	ProPECC PN2/93, Noise Control Ordinance and EIAO Guidance Note NO. 9/2010
S.5.1.1	<u>General Construction Noise Control Measures</u> <ul style="list-style-type: none"> • The Code of Practice on Good Management Practice to Prevent Violation of the Noise Control Ordinance (Chapter 400) (for Construction Industry) published by EPD shall be adopted; • The statutory and non-statutory requirements and guidelines shall be complied with; • Approval for the method of working, equipment and noise mitigation measures intended to be used at the site shall be granted from the Project Engineer before commencing any work; 	To minimize construction noise emissions	Contractor	Work site	Construction Stage	ProPECC PN2/93 and Noise Control Ordinance

Project Profile Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Parties	Location of the measure	When to implement the measure	Relevant requirements or standards for the measure to achieve
	<ul style="list-style-type: none"> • Working methods to minimize the noise impact on the surrounding NSRs shall be formulated and executed, and the implementation of these methods shall be monitored by experienced personnel with suitable training; • Noisy equipment and noisy activities shall be located as far away from the NSRs as is practical; • Unused equipment shall be turned off; • PME should be kept to a minimum and the parallel use of noisy equipment / machinery should be avoided; • All plant and equipment shall be maintained regularly; and • Material stockpiles and other structures shall be effectively utilized as noise barriers, whenever practicable. 					
AIR QUALITY IMPACT						
S.5.1.2	<p><u>Construction Dust Control Measures</u></p> <ul style="list-style-type: none"> • Regular watering to reduce dust emissions from all exposed site surface, particularly during dry weather; • Frequent watering for particularly dusty construction areas and areas close to air sensitive receivers; • Covering of stockpile of excavated dusty materials, if any, with impervious sheeting or spraying with water to maintain the entire surface wet; • Provision of vehicle washing facilities at the entry and exit points of site; • Tarpaulin covering of any dusty materials being transported to and from site by vehicle; • Positioning of construction plant at maximum practicable distance from air sensitive receivers; and • Due to the small size of the works sites and lack of space for stockpiling, excavated materials should be hauled off-site almost immediately. However, in the event of any stockpiled excavated materials, they should be covered with tarpaulin and be removed offsite as soon as practicable to avoid any dust nuisance arising 	To minimize the dust impacts arising from the construction works	Contractor	Work site	Construction Stage	Air Pollution Control (Construction Dust) Regulation

Project Profile Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Parties	Location of the measure	When to implement the measure	Relevant requirements or standards for the measure to achieve
WATER QUALITY IMPACT						
S.5.1.3	<p><u>Construction Water Quality Impact Measures</u></p> <ul style="list-style-type: none"> • Collection of wastewater into a sedimentation tank for treatment before discharge into the public drainage system; • Provision of silt trap and oil interceptor to remove the oil, lubricants, grease, silt, grit and debris from the wastewater prior to discharge to the public stormwater system. The silt traps and oil interceptors should be cleaned and maintained regularly; • Installation of wheel washing facilities to minimize muddy runoff; • Regular maintenance and inspection of drainage systems and erosion control and silt removal facilities; • Management and monitoring of sewage treatment facilities (if any); • Any foul effluent should not be discharged into any public sewer and stormwater drain, unless an effluent discharge permit is obtained under the WPCO by the Contractor; • Coverage of stockpiles of C&D materials (if any) during rainstorms; and • Site toilet facilities, if needed, should be chemical toilets or should have the sewage discharge directed to a foul sewer. 	To reduce water quality impact induced by the construction work	Contractor	Work site	Construction Stage	ProPECC PN1/94; Water Pollution Control Ordinance
WASTE MANAGEMENT						
S.5.1.4	<p><u>Construction Waste Management Measures</u></p> <ul style="list-style-type: none"> • Scrap metals or abandoned equipment should be recycled if possible; • Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner; • The Contractor should adopt a trip ticket system for the disposal of C&D materials to any designated public filling facility and/or landfill. Independent audits of the Contractor and resident site staff will be undertaken to ensure that the correct procedures are being followed; • Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes; and 	To adopt waste management measures in the way of avoiding, minimizing, reusing and recycling so as to reduce waste generation	Contractor	Work site	Construction Stage	Waste Disposal Ordinance (Cap. 354); Waste Disposal (Chemical Waste) (General) Regulation; DEVB TCW No. 6/2010; ETWB TCW No. 19/2005.

Project Profile Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Implementation Parties	Location of the measure	When to implement the measure	Relevant requirements or standards for the measure to achieve
	<ul style="list-style-type: none"> All general refuse should be segregated and stored in enclosed bins or compaction units and waste separation facilities for paper, aluminum cans, plastic bottles etc. should be provided to facilitate reuse or recycling of materials and their proper disposal. 					
LANDSCAPE AND VISUAL IMPACT						
S.5.1.5	<p><u>Landscape and Visual Measures</u></p> <ul style="list-style-type: none"> Clear demarcation of works area to prevent damages to existing trees in close proximity; Protection of all trees planned to be retained onsite; Preserving all affected trees by transplanting where practical. Tree transplanting application and tree removal application shall be submitted for approval in accordance with ETWB TCW 3/2006; and Screening of construction works by hoardings/noise barriers around Works area in visually unobtrusive colors. 	To reduce landscape and visual impact by construction works.	Contractor	Work Site and nearby playground	Construction Stage	EIAO; ETWB TCW No. 3/2006.
