
ID .	Task Name	Duration	Start	Finish										
		Duration	otan		per .	Qtr 4, 201 October November	December	January	Qtr 1, 2016 February	March April	Qtr 2, 2016 May	June	July	Qtr 3, 2016 August
	Sewerage at Chuk Kok Rd, Hiram's Highway, University Road and Clear Water Bay Road	433 days	Mon 2/11/15			/1011/108/105/101/118/1115/12	2 <u>/129/116/1213/120/12</u> 	7/ <u>12 3/1 10/117/124/</u> 	1 31/1 7/2 14/2 21/2 	28/2 6/3 13/3 20/3 27/3 3/4 10/4 17/	4 24/4 1/5 8/5 15/5 22/5	29/5 5/6 12/619/626	;/6 3/7 10/7 17/7 24/7 ; 	31/7 7/8 14/82
2	Sewerage from MH Nos. 1.15 to S5 at University Road & Clear Water Bay Road	433 days	Mon 2/11/15	Sat 7/1/17										
3	Sewerage from MH Nos. PSST155 to S5 at University Road, trenchless (50m long)	172 days	Mon 2/11/15	Thu 21/4/16							•			
4	Excavate & construct Thurst Pit at MH No. PSST155	40 days	Mon 2/11/15	Fri 11/12/15	1	2/11	11/12	1	1			1		
5	Install set-up at Thurst Pit at MH No. PSST155	14 days	Sat 12/12/15	Fri 25/12/15			12/12	25/12				1		
6	Install Segmental Sleeve Pipeline	75 days	Sat 26/12/15	Wed 9/3/16	1		26/12			9/3				1
7	Lay Sewer Pipeline	14 days	Thu 10/3/16	Wed 23/3/16						10/3 23/3				
8	IInfill Grout inside Sleeve Pipe	5 days	Thu 24/3/16	Mon 28/3/16						24/3 28/3				
9	Re-construct Existing Manhole MH No. S5	24 days	Tue 29/3/16	Thu 21/4/16						29/3	21/4			
10 11	Sewerage from MH Nos. PSST151 to PSST155 at University Road (Footpath)-85m long	249 days	Sat 26/12/15	Tue 30/8/16			-					- 		
12	Excavate & construct Thurst Pit at MH No. PSST151	40 days	Sat 26/12/15	Wed 3/2/16			26/12	 	3/2					1
13	Install set-up at Thurst Pit at MH No. PSST151	14 days		Wed 17/2/16	1			1	4/2			1		
14	Install Segmental Sleeve Pipeline	120 days		Thu 16/6/16	i.				18/2			16/6		
15	Lay Sewer Pipeline	25 days		Mon 11/7/16	i i							17/6	11/7	
16	Infill Grout inside Sleeve Pipe	10 days		Thu 21/7/16	1			1					12/7	
17	·				i i								22/7	1
	Construct Manhole No. PSST155 (6.3m deep)	40 days	FII 22/7/10	Tue 30/8/16	i I			1	1			1		
18 19	Sewerage from MH No. MF1.15 to MH No.PSST151 at Clear Water Bay Road (Footpath)-85m long	261 days	Fri 22/4/16	Sat 7/1/17										
20	Install set-up at Thurst Pit at MH No. PSST151	14 days	Fri 22/4/16	Thu 5/5/16						22/4	5/5	 		
21	Install Segmental Sleeve Pipeline	120 days	Fri 6/5/16	Fri 2/9/16							6/5			
22	Lay Sewer Pipeline	25 days	Sat 3/9/16	Tue 27/9/16	1									1
23	IInfill Grout inside Sleeve Pipe	10 days	Wed 28/9/16	Fri 7/10/16	 									1
24	Re-construct Existing Manhole MH No. MF1.15	25 days	Sat 8/10/16	Tue 1/11/16										
25	Construct Manhole No. PSST151 (7 m deep)	55 days	Wed 2/11/16	Mon 26/12/16	i I			1	I I			i I		
26	CCTV of Pipeline (Stage 4)	12 days	Tue 27/12/16	Sat 7/1/17				1				1		1
27					1									
28	Sewerage from MH Nos. PSST149 to PSST147 at Clear Water Bay Road (Carriageway)-93m long	182 days	Mon 9/11/15	Sun 8/5/16										
29	MH Nos. PSST149 to PSST148	48 days	Mon 9/11/15	Sat 26/12/15	 	9/11		26/12				1 		
30	MH Nos. PSST148 to PSST147	134 days	Sun 27/12/15	Sun 8/5/16			27/12				8/5			1
31														
32	Sewerage from MH Nos. PSST147 to PSST140 at Chuk Kok Road (carrigeway)-84m long	141 days	Mon 9/5/16	Mon 26/9/16								 		
33	MH Nos. PSST147 to PSST146	108 days	Mon 9/5/16	Wed 24/8/16				 	1		9/5			1
34	MH Nos. PSST146 to PSST140	33 days	Thu 25/8/16	Mon 26/9/16										25/8
35								1 				1		
36	Sewerage from MH Nos. PSST140 to PSST135 at Chuk Kok Road (carrigeway)_180m long	152 days	Mon 16/11/15	Fri 15/4/16										
37	MH Nos. PSST140 to PSST139		Mon 16/11/15		l.	16/11	i	Í.	i.		i	i.		

Welcome Constuction Co Ltd.



					Detailed Program fo	Sewerage at Clea r Sewage Works	Contra ar Water Bay Road	e Constuction Co act No. DC/2012/0 , Pik Shui Sun Tsu y Road, University	6 en and West of Sai	Kung Town ad & Hiram's H	ighway (Rev. 3)			
ID T	Task Name	Duration	Start	Finish	0+ 4 2045									
					Otr 4, 2015 Per October November 20/9/27/9/4/1011/10/8/11/25/10/1/11/8/11/5/11/22/12:	December	January	Qtr 1, 2016 February	March	April	Qtr 2, 2016 May			Qtr 3, 2016 August
38	MH Nos. PSST139 to PSST138	21 days	Fri 25/12/15	Thu 14/1/1	20/9/2//9/4/10/1/10/0/1/25/10//11/0/11/5/11/2/12	25/12	14/1	131/11 //2 114/2121/212	0/2 0/3 113/3/20/3/27/3	3/4 10/4 17/4 24/	4 1/5 6/5 15/5/22/5/28	1/5 5/6 2/6 9/6 26	1	131/7 7/8 14/82 1/820
39	MH Nos. PSST138 to PSST137	32 days	Fri 15/1/16	Mon 15/2/1			15/1	15/2						
40	MH Nos. PSST137 to PSST136	24 days	Tue 16/2/16	Thu 10/3/1				16/2	10/3					-
41	MH Nos. PSST136 to PSST135	36 days	Fri 11/3/16	Fri 15/4/1					11/3	15/4				
42	CCTV Survey of Pipeline (Stage 1)	3 days	Sat 16/4/16	Mon 18/4/1				1		16/4 👗 18/4				
43													1	1
44	Sewerage from MH Nos. PSST135 to PSST134 at Chuk Kok Rd near Cheng Chek Chee Secondary School -36m long	35 days	Tue 19/4/16	Mon 23/5/1						•				1 1 1
45	MH Nos. PSST135 to PSST134	31 days	Tue 19/4/16	Thu 19/5/1			1	 	 	19/4	19/5		 	1
46	CCTV Survey of Pipeline (Stage 2)	4 days	Fri 20/5/16	Mon 23/5/1							20/5 📩 23/5		 	1
47													- - -	-
48	Sewerage from MH Nos. PSST146 to PSST141 at Hiram's Highway Slip Road (carriageway) - 157m long	339 days	Mon 23/11/15	Wed 26/10/1										
49	MH Nos. PSST143 to PSST142	47 days	Mon 23/11/15	Fri 8/1/1	23/11		8/1	- 					1	1
50	MH Nos. PSST144 to PSST145	88 days	Sat 9/1/16	Tue 5/4/1			9/1			5/4				
51	MH Nos. PSST145 to PSST144	83 days	Wed 6/4/16	Mon 27/6/1					6/4	ı —			27/6	1
52	MH Nos. PSST146 to PSST145	85 days	Tue 28/6/16	Tue 20/9/1								28/6	<u>+</u>	1
53	MH Nos. PSST142 to PSST141	36 days	Wed 21/9/16	Wed 26/10/1				1						1
54	CCTV Survey of Pipeline (Stage 3)	5 days	Thu 27/10/16	Mon 31/10/1										
55								1	 				1	1
56	Sewerage from MH No. PSST141 to Hirams Villas	5 days	Thu 27/10/16	Mon 31/10/1					 					
57	Tapping Sewer to MH No. PSST141	5 days	Thu 27/10/16	Mon 31/10/1										
58													i I I	i I I
59 C	Completion of Sewerage Works	0 days	Sat 7/1/17	Sat 7/1/1			1	1					T T	I I

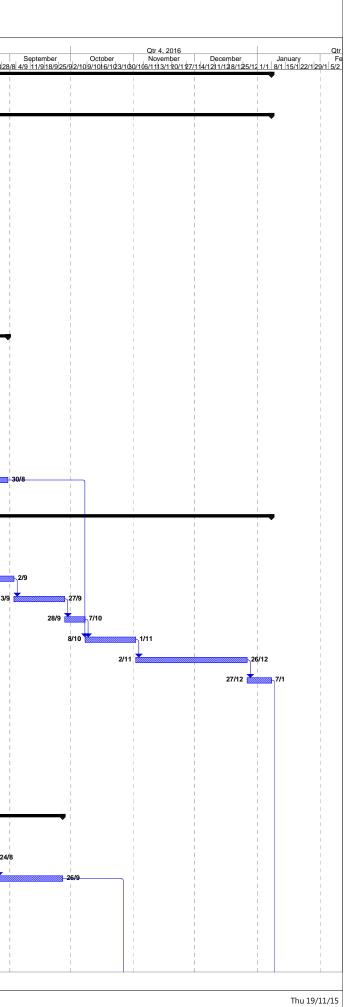
