

# FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



## QUARTERLY ENVIRONMENTAL MONITORING & AUDIT SUMMARY REPORT

September 2019 – November 2019

**Client** : SANG HING – KULY JOINT VENTURE

**Contract Name** : Castle Peak Road Trunk Sewer and Tuen Mun Village Sewerage (Sewage Pumping Station at Lok Chui Street near Castle Peak Villas)

**Contract No.** : DC/2014/01

**EP No.** : EP-068/2000/A

**Title of Project** : Sewage Pumping Stations at Tai Lam Chung Tsuen Luen On San Tsuen, Tai Lam Valley and Lok Chui Street near Castle Peak Villas under the scope of "Tuen Mun Sewerage – Eastern Coastal Sewerage Extension"

**Report No.** : 0367/15/ED/1223

**Prepared by** : Wingo H. W. So

**Reviewed by** : Cyrus C. Y. Lai

**Certified by** :   
Colin K. L. Yung  
Environmental Team Leader  
Fugro Technical Services Limited

10 December 2019



Drainage Services Department  
42/F., Revenue Tower  
5 Gloucester Road  
Wan Chai  
Hong Kong

Attention: Mr Lee Wai Chung

Your reference:

Our reference: HKDSD202/50/106196

Date: 16 December 2019

**BY EMAIL & POST**  
**(email: [wlee@dsd.gov.hk](mailto:wlee@dsd.gov.hk))**

Dear Sirs

Agreement No.: PM 08/2014  
Services for Independent Environmental Checker for  
Construction of Lok Chui Street Sewage Pumping Station  
Verification of Quarterly EM&A Summary Report (September – November 2019)

We refer to email of 10 December 2019 attaching a Quarterly EM&A Summary Report (September – November 2019) for the captioned project prepared by the ET.

We have no comment and hereby verify the captioned report.

Please do not hesitate to contact the undersigned or our Mr Ricky Lau at 2618 2831 should you have any queries.

Yours faithfully  
ANEWR CONSULTING LIMITED

Adi Lee  
Independent Environmental Checker

LYMA/LCCR/csym

# FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



## TABLE OF CONTENTS

|  |          |
|--|----------|
| <b>EXECUTIVE SUMMARY</b>   | <b>1</b> |
| <b>1. INTRODUCTION</b>   | <b>2</b> |
| <b>2. ENVIRONMENTAL MONITORING &amp; AUDIT REQUIREMENTS</b>          | <b>4</b> |
| <b>3. ADVICE ON THE SOLID AND LIQUID WASTE MANAGEMENT STATUS</b>     | <b>5</b> |
| <b>4. ENVIRONMENTAL SITE INSPECTION AND AUDIT</b>                    | <b>6</b> |
| <b>5. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE</b>                 | <b>6</b> |
| <b>6. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES</b> | <b>7</b> |
| <b>7. FUTURE KEY ISSUES</b>  | <b>7</b> |
| <b>8. CONCLUSIONS</b>  | <b>8</b> |

## FIGURES

|          |   |
|----------|---|
| Figure 1 | Site Layout Plan                          |
| Figure 2 | Air Quality and Noise Monitoring Stations |

## LIST OF APPENDICES

|            |  |
|------------|--|
| Appendix A | Construction Programme   |
| Appendix B | Project Organization Chart   |
| Appendix C | Action and Limit Levels for Air Quality and Noise  |
| Appendix D | Air Quality Monitoring Data and Graphical Presentations  |
| Appendix E | Noise Monitoring Data and Graphical Presentations  |
| Appendix F | Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions |
| Appendix G | Implementation Status of Environmental Mitigation Measures   |
| Appendix H | Monthly Summary of Waste Flow Table  |

**EXECUTIVE SUMMARY**

- i. This is the 15<sup>th</sup> Quarterly Environmental Monitoring Audit (EM&A) Summary Report, it presents the environmental monitoring and audit works for the period from 1 September 2019 to 30 November 2019.

**Construction Activities for the Reporting Period**

- ii. During this reporting period, the principal work activities within the site included:

|   |
|---|
| <b>September 2019</b>                         |
| • Laid UU and construct road access           |
| <b>October 2019</b>                           |
| • Construct road access and recycle timber    |
| <b>November 2019</b>                          |
| • Laying paving block and construct draw-pits |

**Breaches of Action and Limit Levels for Air Quality**

- iii. No Action or Limit Level Exceedance of 1-hr TSP monitoring was recorded in the reporting period.

**Breaches of Action and Limit Levels for Noise**

- iv. No exceedance was recorded at all monitoring stations in the reporting period.

**Complaint, Notifications of Summons and Successful Prosecutions**

- v. No complaints, notification of summons or successful prosecutions were received in the reporting period.

**Reporting Change**

- vi. There was no reporting change required in the reporting period.

**Future Key Issues**

- vii. Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirements. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.



## 1. INTRODUCTION

### 1.1 Background

- 1.1.1 Contract No. DC/2014/01 – Castle Peak Road Trunk Sewer and Tuen Mun Village Sewerage (“the Project”) includes the construction of a sewage pumping station at Lok Chui Street near Castle Peak Villas as shown in **Figure 1**.
- 1.1.2 The environmental impact assessment (EIA) report (Tuen Mun Sewerage - Eastern Coastal Sewerage Extension) – EIA Report (Register No. AEIAR-034/2000) for the Project was approved by Environmental Protection Department (EPD) dated 7 June 2000. The EIA Report involves the construction of four sewage pumping stations at Tai Lam Chung Tsuen, Luen On San Tsuen, Tai Lam Valley and Lok Chui Street near Castle Peak Villas. The scope of this EM&A Manual focuses on the Sewage Pumping Station at Lok Chui Street near Castle Peak Villas in the EIA Report. The Project is designated under Schedule 2, section F3(b) and Q1 of the Environmental Impact Assessment Ordinance (EIAO). EPD subsequently issued the Environmental Permit (EP) EP- 068/2000 on 25 July 2000.
- 1.1.3 A Register of Change to Environmental Permit was submitted to EPD to register any change to the conditions in the EP for adoption of the latest design of the Pumping Station at Lok Chui Street and justify that the latest changes would not violate the conditions as stated in the approved EIA Report and EP based on the latest engineering design information. A Variation of Environmental Permit (VEP) EP-068/2000/A was issued on 10 April 2015 and it is the current permit for the Project.
- 1.1.4 The amended EP (EP-068/2000/A) is the current permit for the Project.
- 1.1.5 In accordance to EP-068/2000/A Condition 2.3 and 2.4, an updated EM&A Manual was duly certified by ETL and verified by IEC and submitted to EPD for approval on 18 January 2016.
- 1.1.6 The construction phase and EM&A programme of the Project commenced on 29 February 2016.
- 1.1.7 This is the 15<sup>th</sup> Quarterly Environmental Monitoring Audit (EM&A) Summary Report, it presents the environmental monitoring and audit works for the period from 1 September 2019 to 30 November 2019.



**1.2 Project Organization**

1.2.1 The Project Organization structure is shown in **Appendix B**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

| Party                                      | Position                          | Name                | Telephone | Fax       |
|--|-----------------------------------|---------------------|-----------|-----------|
| Drainage Services Department, HKSAR (DSD)  | Project Management                | Mr. Lee Wai Chung   | 2594 7265 | 2827 8526 |
| Engineer/Engineer's Representative (AECOM) | Resident Engineer                 | Ms. Jacqueline Chan | 3127 5103 | 2441 1755 |
| Independent Environmental Checker (ANEWR)  | Independent Environmental Checker | Mr. Adi Lee         | 2618 2836 | 3007 8648 |
| Contractor (SKLV)                          | Site Agent                        | Mr. Alan Lo         | 2674 3888 | 2674 6688 |
|  | Environmental Officer             | Mr. Billy Wong      |           |           |
| Environmental Team (FTS)                   | Environmental Team Leader         | Mr. Colin Yung      | 3565 4114 | 3565 4160 |

**1.3 Construction Programme and Activities**

1.3.1 The construction phase of the Project under the EP commenced on 29 February 2016.

1.3.2 The construction programme of the Project is shown in **Appendix A**.

**1.4 Works undertaken during the Reporting Period**

1.4.1 During this reporting period, the principal work activities within the site included:

|   |
|---|
| <b>September 2019</b>                         |
| • Laid UU and construct road access           |
| <b>October 2019</b>                           |
| • Construct road access and recycle timber    |
| <b>November 2019</b>                          |
| • Laying paving block and construct draw-pits |

**1.5 Status of Environmental Licences, Notification and Permits**

1.5.1 A summary of the relevant permits, licences and/or notifications on environmental protection for this Contract is presented in **Table 1.2**.

Table 1.2 Status of Environmental Licences, Notification and Permits

| Permit / Direction / License                       | Ref No            | Valid From | Valid Till |
|--|-------------------|------------|------------|
| Environmental Permit                               | EP-068/2000/A     | 10/04/2015 | N/A        |
| Notification of Works Under APCO                   | 391923            | 06/08/2015 | N/A        |
| Wastewater Discharge Licence                       | WT00022654-2015   | 23/10/2015 | 31/10/2020 |
| Registration as a Chemical Waste Producer          | 5111-421-S3879-01 | 02/09/2015 | N/A        |
| Billing Account for Disposal of Construction Waste | 7022922           | 06/08/2015 | N/A        |



**2. ENVIRONMENTAL MONITORING & AUDIT REQUIREMENTS**

**2.1 Monitoring Parameters and Monitoring Locations**

2.1.1 In accordance with the updated EM&A Manual, monitoring of the 1 hourly average of Total Suspended Particulates (TSP) levels for air quality and the A-weighted equivalent continuous sound pressure level Leq (30min) for the time period between 0700-1900 hours on normal weekdays for noise impact. The monitoring locations are shown in **Figure 2**.

**2.2 Monitoring Methodology and Calibration**

2.2.1 Monitoring equipment were conducted and calibrated regularly in accordance with the updated EM&A Manual. Copies of calibration certificates are attached in the appendices of the corresponding Monthly EM&A Reports.

**2.3 Environmental Quality Performance Limits (Action and Limit Levels)**

2.3.1 The adopted Action and Limit Levels for air quality impact and noise monitoring are presented in **Appendix C**.

**2.4 Environmental Mitigation Measures**

2.4.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Reports, the EP and the EM&A Manuals. The implementation status of the mitigation measures during the reporting period is summarized in **Appendix G**.

**2.5 Results and Observations**

2.5.1 The weather conditions during the monitoring are presented in the Appendices of the corresponding Monthly EM&A Reports.

2.5.2 The monitoring data of 1-hr TSP are summarized in **Table 2.1**. Detailed monitoring data are presented in **Appendix D**.

Table2.1 Summary of 1-hr TSP Monitoring Results

| Reporting Months | Monitoring Station | Average ( $\mu\text{g}/\text{m}^3$ ) | Range ( $\mu\text{g}/\text{m}^3$ ) | Action Level ( $\mu\text{g}/\text{m}^3$ ) | Limit Level ( $\mu\text{g}/\text{m}^3$ ) |
|------------------|--------------------|--------------------------------------|------------------------------------|---|--|
| September 2019   | LC6a               | 57                                   | 38-73                              | 344                                       | 500                                      |
|                  | LC9                | 48                                   | 29-65                              | 335                                       |  |
| October 2019     | LC6a               | 74                                   | 34-182                             | 344                                       |  |
|                  | LC9                | 32                                   | 66-174                             | 335                                       |  |
| November 2019    | LC6a               | 83                                   | 39-135                             | 344                                       |  |
|                  | LC9                | 85                                   | 46-128                             | 335                                       |  |



2.5.3 The noise monitoring data are summarized in **Table 2.2**. Detailed monitoring data are presented in **Appendix E**.

**Table 2.2 Summary of Noise Impact Monitoring Results**

| Reporting Month | Monitoring Station | Leq <sub>(30min)</sub> Range, dB(A) |           | Leq <sub>(30min)</sub> Limit Level, dB(A) |
|-----------------|--------------------|-------------------------------------|-----------|---|
|                 |                    | Measured                            | Corrected |   |
| September 2019  | LC6a <sup>1</sup>  | 64-72                               | 59-67     | 75  |
|                 | LC9                | 58-72                               | N.A       |   |
| October 2019    | LC6a <sup>1</sup>  | 64-70                               | 59-65     |   |
|                 | LC9                | 51-65                               | N.A       |   |
| November 2019   | LC6a <sup>1</sup>  | 61-69                               | 56-64     |   |
|                 | LC9                | 51-67                               | N.A       |   |

Note:

- Leq<sub>(30min)</sub> was measured at day-time (0700-1900) on normal weekdays.
- 1) A distance correction of -5dB(A) has been applied in monitoring data of LC6a according to baseline monitoring report (Appendix G).

2.5.4 No Action or Limit Level Exceedance of 1-hr TSP monitoring was recorded in the reporting period.

2.5.5 No Action or Limit Level Exceedance of noise monitoring was recorded in the reporting period.

**2.6 Other factor influencing the monitoring results**

2.6.1 There were no other noticeable external factors generally affecting the monitoring results in this reporting period.

**3. ADVICE ON THE SOLID AND LIQUID WASTE MANAGEMENT STATUS**

3.1.1 The Contractor has been registered as a chemical waste producer for the Project. Construction and demolition (C&D) material sorting was carried out on site. Receptacles were available for general refuse collection.

3.1.2 Monthly summary of waste flow table is detailed in **Appendix H**.





**4. ENVIRONMENTAL SITE INSPECTION AND AUDIT**

**4.1 Site Inspection**

- 4.1.1 Weekly site inspections and bi-weekly landscape and visual impact inspections were carried out to monitor the implementation of proper environmental pollution control and mitigation measures for the Project.
- 4.1.2 In the reporting period, site inspections were carried out on 5, 12, 19 and 26 September 2019, 3, 10, 17, 24 and 31 October 2019 and 7, 15, 21 and 28 November 2019. The landscape and visual impact inspections were carried out on 4 and 19 September 2019, 2, 17 and 31 October 2019 and 14 and 28 November 2019.
- 4.1.3 Detailed of site inspections during the reporting period are summarized in the appendices of the corresponding Monthly EM&A Reports.

**5. ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE**

**5.1 Environmental Exceedance**

- 5.1.1 No Action or Limit Level Exceedance of 1-hr TSP monitoring was recorded in the reporting period.
- 5.1.2 No Action or Limit Level Exceedance of noise monitoring was recorded in the reporting period.
- 5.1.3 The summary of noncompliance (exceedances) of the environmental quality performance limits (Action and Limit levels) are shown in **Table 5.1**:

Table 5.1 Summary of noncompliance (exceedances)

| Parameter                             | No. of Exceedance |             | No. of Exceedance due to the Project |             | Cumulative Project-to-Date |
|---------------------------------------|-------------------|-------------|--------------------------------------|-------------|----------------------------|
|                                       | Action Level      | Limit Level | Action Level                         | Limit Level |                            |
| 1-hr TSP                              | 0                 | 0           | 0                                    | 0           | 0                          |
| Noise<br>Leq <sub>(30min)</sub> dB(A) | 0                 | 0           | 0                                    | 0           | 0                          |

**5.2 Complaints, Notification of Summons and Successful Prosecution**

- 5.2.1 No complaints, notification of summons or successful prosecutions were received in the reporting period.
- 5.2.2 Cumulative complaint log, summaries of complaints, notification of summons and successful prosecutions are presented in **Appendix F**.

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



---

## 6. IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

### 6.1 Implementation Status

- 6.1.1 The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Reports, the EP and the EM&A Manuals. The implementation status of the mitigation measures during the reporting period is summarized in **Appendix G**.
- 6.1.2 Based on the monitoring results and the implementation status of the mitigation measures during the reporting period, it is considered that the environmental mitigation measures implemented by the Contractor in the reporting period are effective.

## 7. FUTURE KEY ISSUES

- 7.1.1 Potential environmental impacts due to the construction activities, including air quality, noise, water quality, waste, landscape and visual, will be monitored or reviewed. The ET will continue to implement the environmental monitoring & audit programme in accordance with the EM&A Manual and Environmental Permit requirement. The recommended environmental mitigation measures shall be implemented on site and regular inspections as required will be carried out to ensure that the environmental conditions are acceptable.

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



### 8. CONCLUSIONS

- 8.1.1 The construction phase and EM&A programme of the Project commenced on 29 February 2016.
- 8.1.2 No Action or Limit Level Exceedance of 1-hr TSP monitoring was recorded in the reporting period.
- 8.1.3 No Action or Limit Level Exceedance of noise monitoring was recorded in the reporting period.
- 8.1.4 In the reporting period, site inspections were carried out on 5, 12, 19 and 26 September 2019, 3, 10, 17, 24 and 31 October 2019 and 7, 15, 21 and 28 November 2019. The landscape and visual impact inspections were carried out on 4 and 19 September 2019, 2, 17 and 31 October 2019 and 14 and 28 November 2019.
- 8.1.5 No complaints, notification of summons or successful prosecutions were received in the reporting period.

## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.


Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Figure 1**

### **Project General Layout**

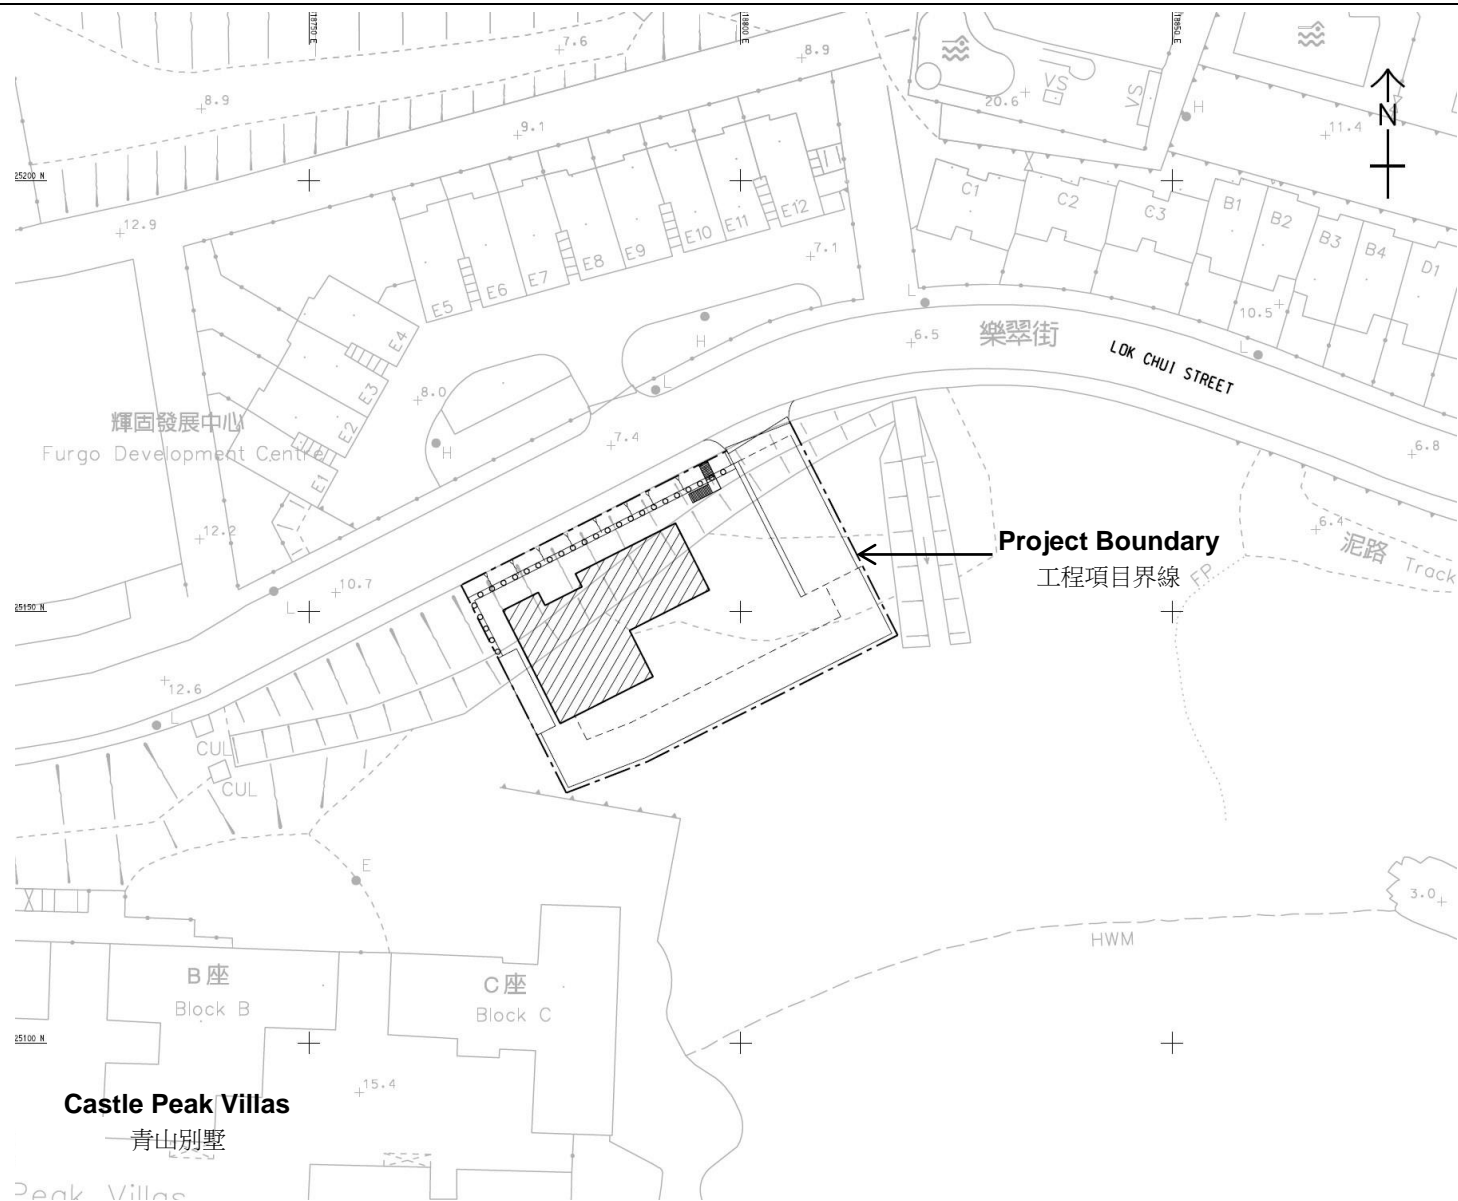

**Location of the Proposed Sewage Pumping Station at Lok Chui Street near Castle Peak Villas**  
 位於樂翠街近青山別墅的擬建污水泵水站

Figure 1

## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.


Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Figure 2**

#### **Air and Noise Monitoring Locations**

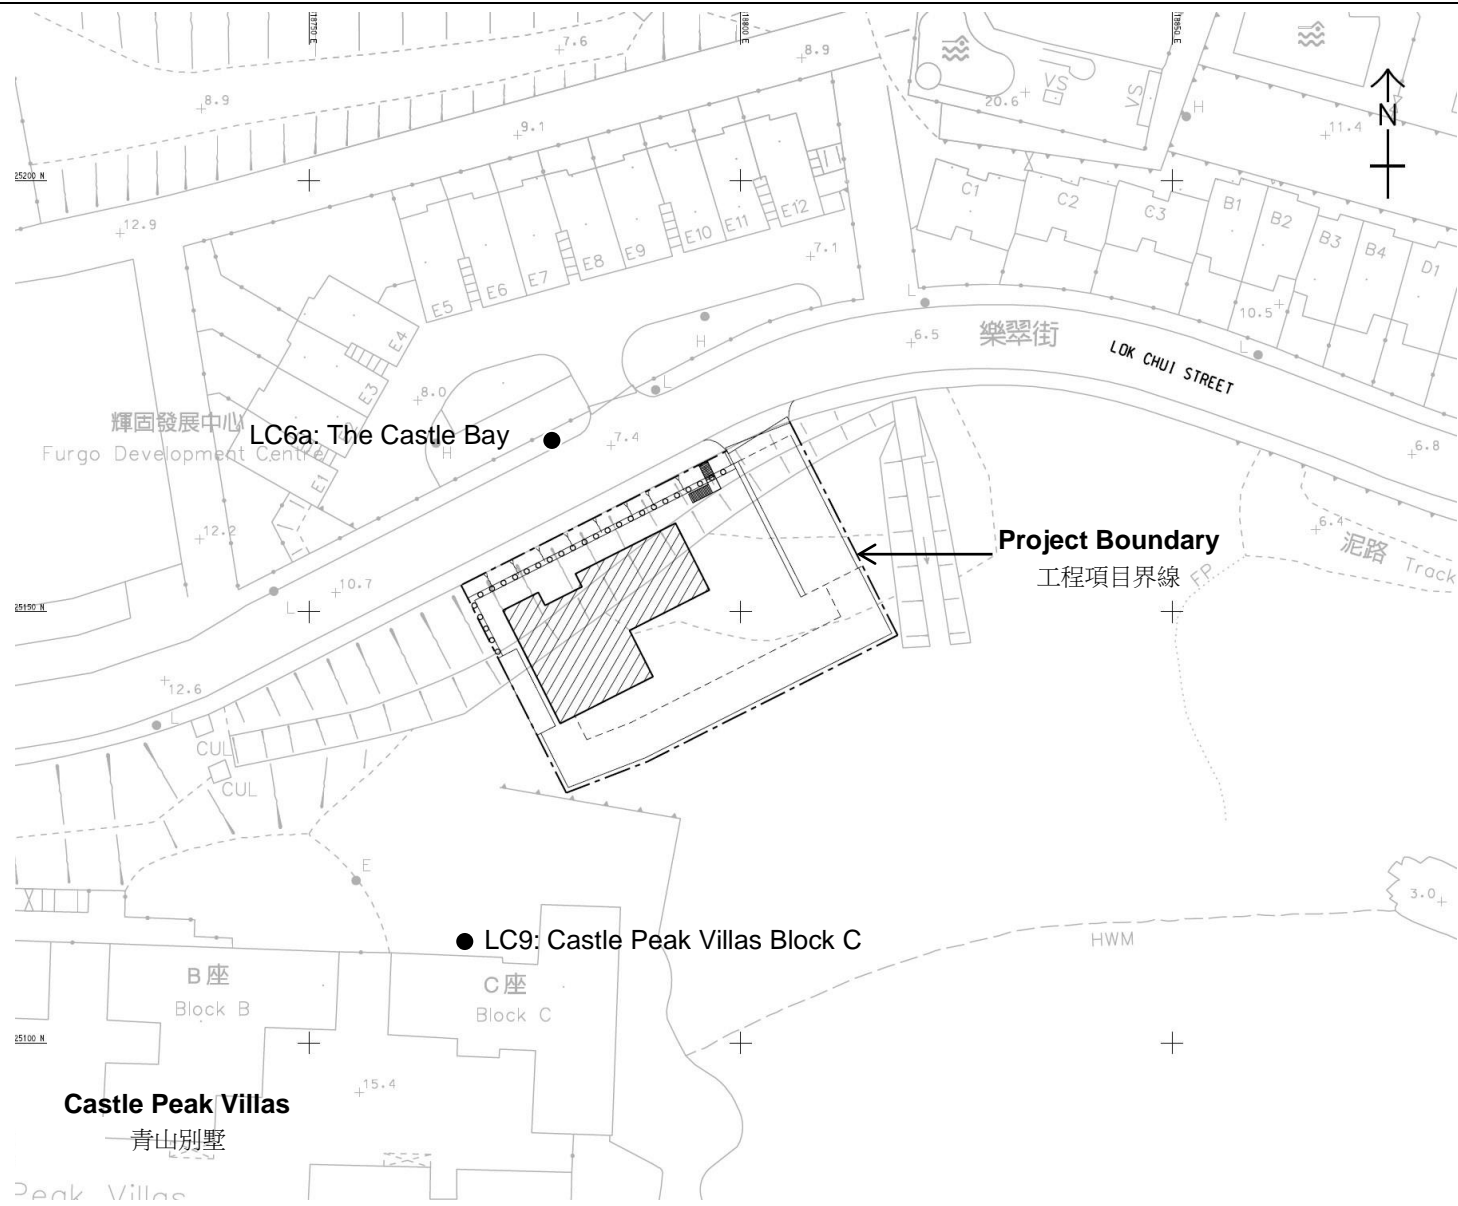

Air and Noise Monitoring Locations

Figure 2

# FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



LC6a: The Castle Bay






LC9: Castle Peak Villas Block C



**Note:**

1) LC6a: The air and noise monitoring station is set at a point 1m from the exterior of the sensitive receiver fence wall, and set at a position 1.2m above ground. Façade measurement will be carried out for noise monitoring.

2) LC9: The air monitoring station is set at the top of parapet wall of sensitive receivers building and the noise monitoring station is set at a point 1m from the exterior of the sensitive receivers building façade and set at a position 5m above the ground.

- Legend:
-  Proposed Air Monitoring Location
  -  Proposed Noise Monitoring Location
  -  1m from the exterior building façade



## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Appendix A**

### **Construction Programme**

| ID   | Task Name   | Baseline Duration | Duration   | Baseline Start | Baseline Finish | Actual Start | Actual Finish | % Complete | Start        | Finish       | Predecessors           | 15/10/15 | 2016 Q4 | 2017 Q1 | 2017 Q2 | 2017 Q3 | 2017 Q4 | 2018 Q1 | 2018 Q2 | 2018 Q3 | 2018 Q4 | 2019 Q1 | 2019 Q2 | 2019 Q3 | 2019 Q4 | 2020 Q1 | 2020 Q2 | 2020 Q3 | 2020 Q4 |  |  |  |  |
|------|---|-------------------|------------|----------------|-----------------|--------------|---------------|------------|--------------|--------------|------------------------|----------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|---------|--|--|--|--|
| 1301 | Trial pits proposal   | 180 days          | 180 days   | Sun 18/10/15   | Thu 14/4/16     | Sun 18/10/15 | Thu 14/4/16   | 100%       | Sun 18/10/15 | Thu 14/4/16  | 1297SS,1298SS          |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1302 | Design of Temporary Work  | 30 days           | 30 days    | Sat 16/1/16    | Mon 15/2/16     | Fri 16/9/16  | Sun 16/10/16  | 100%       | Fri 16/9/16  | Sun 16/10/16 | 1303SF                 |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1303 | Submission of Design Temporary Work   | 0 days            | 351 days   | Mon 15/2/16    | Mon 15/2/16     | Sun 16/10/16 | Mon 2/10/17   | 100%       | Sun 16/10/16 | Mon 2/10/17  | 1314SF-60 days         |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1304 | Hong Fai Road   | 240 days          | 240 days   | Fri 18/8/17    | Sat 14/4/18     | Wed 8/2/17   | Thu 5/10/17   | 100%       | Wed 8/2/17   | Thu 5/10/17  |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1305 | From Manhole 1903 to 0716   | 240 days          | 240 days   | Fri 18/8/17    | Sat 14/4/18     | Wed 8/2/17   | Thu 5/10/17   | 100%       | Wed 8/2/17   | Thu 5/10/17  | 1282FS-210 days        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1306 | From Manhole 0703 to 0701   | 25 days           | 25 days    | Wed 21/3/18    | Sat 14/4/18     | Mon 11/9/17  | Thu 5/10/17   | 100%       | Mon 11/9/17  | Thu 5/10/17  | 1305FF                 |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1307 | Connection to Siu Lam Tsuen Road From Manhole 0716 to 0718  | 35 days           | 35 days    | Sun 11/3/18    | Sat 14/4/18     | Fri 1/9/17   | Thu 5/10/17   | 100%       | Fri 1/9/17   | Thu 5/10/17  | 1305FF                 |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1308 |   |                   |            |                |                 |              |               |            |              |              |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1309 | EOT Claim 020 - Delay for construction of CSD Married Staff Quarter (On going event)                  | 0 days?           | 1112 days? | NA             | NA              | NA           | NA            | 0%         | Thu 15/12/16 | Tue 31/12/19 |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1310 | Pending ER confirm works details  | 0 days?           | 382 days?  | NA             | NA              | NA           | NA            | 0%         | Thu 15/12/16 | Sun 31/12/17 |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1311 | Design and Endorsement of TTA drawings and TTA Implementation   | 0 days?           | 150 days   | NA             | NA              | NA           | NA            | 0%         | Mon 1/1/18   | Wed 30/5/18  | 1310                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1312 | Additional construction time due to revised TTA implementation period                                 | 0 days?           | 300 days   | NA             | NA              | NA           | NA            | 0%         | Thu 7/3/19   | Tue 31/12/19 | 1319                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1313 | Access Road Leading to CSD Married Staff Quarter  | 280 days          | 280 days   | Fri 15/4/16    | Thu 19/1/17     | NA           | NA            | 0%         | Thu 31/5/18  | Wed 6/3/19   |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1314 | From Manhole 1104 to Manhole 1110   | 45 days           | 45 days    | Fri 15/4/16    | Sun 29/5/16     | NA           | NA            | 0%         | Thu 31/5/18  | Sat 14/7/18  | 1301SS+180 days,1311   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1315 | From Manhole 1201 to Manhole 1203   | 25 days           | 25 days    | Mon 30/5/16    | Thu 23/6/16     | NA           | NA            | 0%         | Sun 15/7/18  | Wed 8/8/18   | 1314                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1316 | From Manhole 2001 to Manhole 1203   | 20 days           | 20 days    | Fri 24/6/16    | Wed 13/7/16     | NA           | NA            | 0%         | Thu 9/8/18   | Tue 28/8/18  | 1315                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1317 | From Manhole 1203 to Manhole 1110   | 20 days           | 20 days    | Thu 14/7/16    | Tue 2/8/16      | NA           | NA            | 0%         | Wed 29/8/18  | Mon 17/9/18  | 1316                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1318 | From Manhole 1110 to Manhole 1118   | 100 days          | 100 days   | Wed 3/8/16     | Thu 10/11/16    | NA           | NA            | 0%         | Tue 18/9/18  | Wed 26/12/18 | 1317                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1319 | From Manhole 1118 to Manhole 1122   | 70 days           | 70 days    | Fri 11/11/16   | Thu 19/1/17     | NA           | NA            | 0%         | Thu 27/12/18 | Wed 6/3/19   | 1318                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1320 | Siu Lam Road  | 20 days           | 20 days    | Mon 26/3/18    | Sat 14/4/18     | NA           | NA            | 0%         | Tue 31/7/18  | Sun 19/8/18  |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1321 | Connection From Manhole 0901 to 0721 after trenchless   | 20 days           | 20 days    | Mon 26/3/18    | Sat 14/4/18     | NA           | NA            | 0%         | Tue 31/7/18  | Sun 19/8/18  | 1023SS,1049,1245       |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1322 | CCTV inspection   | 0 days?           | 60 days    | NA             | NA              | NA           | NA            | 0%         | Sat 2/11/19  | Tue 31/12/19 | 1323FF                 |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1323 | Completion of Section 9C  | 0 days            | 0 days     | Sat 14/4/18    | Sat 14/4/18     | NA           | NA            | 0%         | Tue 31/12/19 | Tue 31/12/19 | 1321,1305,1306,1307,12 |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1324 | Section 9C - Inclement Weather Granted (EOT Claim No. 3.18, up to 31 July 2017)                       | 0 days?           | 53 days    | NA             | NA              | NA           | NA            | 0%         | Wed 1/1/20   | Sat 22/2/20  | 1323                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1325 |   |                   |            |                |                 |              |               |            |              |              |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1326 | Duration of Section 11A - Lok Chui Street Sewage Pumping Station                                      | 929 days          | 929 days   | Mon 20/7/15    | Fri 2/2/18      | Mon 20/7/15  | NA            | 93%        | Mon 20/7/15  | Fri 2/2/18   |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1327 | Inclement Weather Granted (EOT Claim No. 3.18, up to 31 July 2017)                                    | 0 days?           | 58 days    | NA             | NA              | NA           | NA            | 0%         | Sat 3/2/18   | Sun 1/4/18   | 1326                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1328 | Granted under EOT Order 11 (Delayed Possession of Site)   | 0 days?           | 40 days    | NA             | NA              | NA           | NA            | 0%         | Mon 2/4/18   | Fri 11/5/18  | 1327                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1329 | Additional Time for Completion  | 0 days?           | 347 days   | NA             | NA              | NA           | NA            | 0%         | Mon 11/6/18  | Thu 23/5/19  | 1328,1456FF            |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1330 |   |                   |            |                |                 |              |               |            |              |              |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1331 | EOT claim - Change of Design at LCS SPS (Double roof slab)  | 0 days?           | 326 days   | NA             | NA              | Mon 7/8/17   | NA            | 0%         | Mon 7/8/17   | Thu 28/6/18  |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1332 | Revised construction details from ER  | 0 days?           | 0 days     | NA             | NA              | Mon 7/8/17   | Mon 7/8/17    | 100%       | Mon 7/8/17   | Mon 7/8/17   |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1333 | Additional roof slab of transformer room  | 0 days?           | 45 days    | NA             | NA              | NA           | NA            | 0%         | Tue 15/5/18  | Thu 28/6/18  | 1332,1432              |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1334 |   |                   |            |                |                 |              |               |            |              |              |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1335 | EOT Claim - Additional Works in Transformer Room at Lok Chui Street SPS                               | 0 days?           | 399 days   | NA             | NA              | Thu 26/10/17 | NA            | 22%        | Thu 26/10/17 | Wed 28/11/18 |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1336 | Revised construction details from ER  | 0 days?           | 0 days     | NA             | NA              | Thu 26/10/17 | Thu 26/10/17  | 100%       | Thu 26/10/17 | Thu 26/10/17 |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1337 | Additional construction time due to revised details (ie. Box out, pump sump, additional wall opening) | 0 days?           | 90 days    | NA             | NA              | NA           | NA            | 0%         | Sat 20/1/18  | Thu 19/4/18  | 1336,1431              |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1338 | Laying additional DN100 DI drain pipe   | 0 days?           | 5 days     | NA             | NA              | NA           | NA            | 0%         | Fri 20/4/18  | Tue 24/4/18  | 1337                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1339 | Additional plastic chain storage box  | 0 days?           | 366 days   | NA             | NA              | NA           | NA            | 0%         | Thu 26/10/17 | Fri 26/10/18 |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1340 | Procurement   | 0 days?           | 90 days    | NA             | NA              | NA           | NA            | 0%         | Thu 26/10/17 | Tue 23/1/18  | 1336                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1341 | Fabrication and delivery  | 0 days?           | 90 days    | NA             | NA              | NA           | NA            | 0%         | Wed 24/1/18  | Mon 23/4/18  | 1340                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1342 | Installation on site  | 0 days?           | 5 days     | NA             | NA              | NA           | NA            | 0%         | Mon 22/10/18 | Fri 26/10/18 | 1341,1445              |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1343 | Additional CLP single door  | 0 days?           | 380 days   | NA             | NA              | Thu 26/10/17 | NA            | 22%        | Thu 26/10/17 | Fri 9/11/18  |                        |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1344 | Procurement   | 0 days?           | 90 days    | NA             | NA              | Thu 26/10/17 | NA            | 67%        | Thu 26/10/17 | Tue 23/1/18  | 1336                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |
| 1345 | Prepare and submission of shop drawing  | 0 days?           | 60 days    | NA             | NA              | NA           | NA            | 0%         | Wed 24/1/18  | Sat 24/3/18  | 1344                   |          |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |         |  |  |  |  |

Project: Rolling Programme (Nov 2017)  
 Date: 28 Nov 2017  
 EOT Entitlement Programme based on Master Programme (Rev 0-A)


|                        |  |                    |  |                         |  |                              |  |                    |
|------------------------|--|--------------------|--|-------------------------|--|------------------------------|--|--------------------|
| Task                   |  | Critical Split     |  | Rolled Up Task          |  | Rolled Up Baseline Milestone |  | Project Summary    |
| Task Progress          |  | Baseline           |  | Rolled Up Critical Task |  | Rolled Up Progress           |  | Group By Summary   |
| Critical Task          |  | Milestone          |  | Rolled Up Milestone     |  | Split                        |  | Inactive Task      |
| Critical Task Progress |  | Baseline Milestone |  | Baseline Summary        |  | Baseline Split               |  | Inactive Milestone |
| Critical               |  | Summary            |  | Rolled Up Baseline      |  | External Tasks               |  | Deadline           |





| ID   | Task Name  | Baseline Duration | Duration  | Baseline Start | Baseline Finish | Actual Start | Actual Finish | % omplet | Start        | Finish       | Predecessors            | 15 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 | Q1 | Q2 | Q3 | Q4 |
|------|--|-------------------|-----------|----------------|-----------------|--------------|---------------|----------|--------------|--------------|-------------------------|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|----|
| 1441 | Expoxy coating   | 10 days           | 10 days   | Mon 30/10/17   | Wed 8/11/17     | NA           | NA            | 0%       | Fri 17/8/18  | Sun 26/8/18  | 1439                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1442 | Skirting   | 14 days           | 14 days   | Thu 9/11/17    | Wed 22/11/17    | NA           | NA            | 0%       | Mon 27/8/18  | Sun 9/9/18   | 1441                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1443 | Granlithic screen and epoxy coating floor screen                               | 14 days           | 14 days   | Thu 23/11/17   | Wed 6/12/17     | NA           | NA            | 0%       | Mon 10/9/18  | Sun 23/9/18  | 1442                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1444 | Painting on ceiling  | 14 days           | 14 days   | Thu 7/12/17    | Wed 20/12/17    | NA           | NA            | 0%       | Mon 24/9/18  | Sun 7/10/18  | 1443                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1445 | Installation of lourves and Doors  | 14 days           | 14 days   | Thu 21/12/17   | Wed 3/1/18      | NA           | NA            | 0%       | Mon 8/10/18  | Sun 21/10/18 | 1444                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1446 | Ladder and Handrail  | 14 days           | 14 days   | Thu 4/1/18     | Wed 17/1/18     | NA           | NA            | 0%       | Mon 28/1/19  | Sun 10/2/19  | 1445,1354,1358,1373,138 |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1447 | Cover to cable trench  | 25 days           | 25 days   | Thu 7/12/17    | Sun 31/12/17    | NA           | NA            | 0%       | Mon 28/1/19  | Thu 21/2/19  | 1443,1354,1358,1373,138 |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1448 | cement sand screen for roofing system  | 20 days           | 20 days   | Mon 25/12/17   | Sat 13/1/18     | NA           | NA            | 0%       | Fri 15/2/19  | Wed 6/3/19   | 1447FS-7 days,1342      |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1449 | Roofing system   | 20 days           | 20 days   | Sun 14/1/18    | Fri 2/2/18      | NA           | NA            | 0%       | Thu 7/3/19   | Tue 26/3/19  | 1448                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1450 | Water test of the roof   | 0 days?           | 7 days    | NA             | NA              | NA           | NA            | 0%       | Wed 20/3/19  | Tue 26/3/19  | 1449FF                  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1451 |  |                   |           |                |                 |              |               |          |              |              |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1452 | Installation of watermain  | 28 days           | 28 days   | Sat 6/1/18     | Fri 2/2/18      | NA           | NA            | 0%       | Fri 7/9/18   | Thu 4/10/18  | 1484,1485,1486          |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1453 | Installation of irrigation system within the permise of the building           | 0 days?           | 14 days   | NA             | NA              | NA           | NA            | 0%       | Fri 21/9/18  | Thu 4/10/18  | 1452FF                  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1454 |  |                   |           |                |                 |              |               |          |              |              |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1455 | Completion of Section 11A  | 0 days            | 0 days    | Fri 2/2/18     | Fri 2/2/18      | NA           | NA            | 0%       | Tue 26/3/19  | Tue 26/3/19  | 1449                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1456 | Inclement Weather Granted (EOT Claim No. 3.18, up to 31 July 2017)             | 0 days?           | 58 days   | NA             | NA              | NA           | NA            | 0%       | Wed 27/3/19  | Thu 23/5/19  | 1455                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1457 |  |                   |           |                |                 |              |               |          |              |              |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1458 | Duration of Section 11B - Lok Chui Street Sewage Pumping Station               | 1189 days         | 1189 days | Mon 20/7/15    | Sat 20/10/18    | Mon 20/7/15  | NA            | 73%      | Mon 20/7/15  | Sat 20/10/18 |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1459 | Inclement Weather Granted (EOT Claim No. 3.18, up to 31 July 2017)             | 0 days?           | 59 days   | NA             | NA              | NA           | NA            | 0%       | Sun 21/10/18 | Tue 18/12/18 | 1458                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1460 | Granted under EOT Order 11 (Delayed Possession of Site)                        | 0 days?           | 39 days   | NA             | NA              | NA           | NA            | 0%       | Wed 19/12/18 | Sat 26/1/19  | 1459                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1461 | Additional Time for Completion   | 0 days?           | 348 days  | NA             | NA              | NA           | NA            | 0%       | Tue 26/2/19  | Sat 8/2/20   | 1504FF,1460             |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1462 |  |                   |           |                |                 |              |               |          |              |              |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1463 | Section 11B - Lok Chui street Sewage Pumping Station - E&M and Remaining Works | 1189 days         | 1606 days | Mon 20/7/15    | Sat 20/10/18    | Mon 20/7/15  | NA            | 8%       | Mon 20/7/15  | Wed 11/12/19 |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1464 | Portion 11 - Time of Possession of Site  | 90 days           | 90 days   | Mon 20/7/15    | Sat 17/10/15    | Mon 20/7/15  | Sat 17/10/15  | 100%     | Mon 20/7/15  | Sat 17/10/15 |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1465 |  |                   |           |                |                 |              |               |          |              |              |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1466 | External Works & External Finishes   | 145 days          | 143 days  | Mon 11/9/17    | Fri 2/2/18      | NA           | NA            | 0%       | Tue 17/4/18  | Thu 6/9/18   |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1467 | Lagging wall and capping beam on soldier piles                                 | 95 days           | 95 days   | Mon 11/9/17    | Thu 14/12/17    | NA           | NA            | 0%       | Tue 15/5/18  | Fri 17/8/18  | 1432                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1468 | Backfilling to ground floor slab   | 60 days           | 60 days   | Mon 11/9/17    | Thu 9/11/17     | NA           | NA            | 0%       | Tue 15/5/18  | Fri 13/7/18  | 1432                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1469 | Installation of Emergency overflow pipe  | 25 days           | 25 days   | Mon 11/9/17    | Thu 5/10/17     | NA           | NA            | 0%       | Tue 15/5/18  | Fri 8/6/18   | 1432                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1470 | Dismantling of hoarding  | 0 days?           | 28 days   | NA             | NA              | NA           | NA            | 0%       | Tue 17/4/18  | Tue 15/5/18  | 1471SF                  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1471 | Retaining Wall & Mass concrete wall  | 75 days           | 75 days   | Mon 11/9/17    | Fri 24/11/17    | NA           | NA            | 0%       | Tue 15/5/18  | Sat 28/7/18  |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1472 | Frist bay retaining wall   | 0 days?           | 20 days   | NA             | NA              | NA           | NA            | 0%       | Tue 15/5/18  | Sun 3/6/18   | 1432                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1473 | Second bay retaining wall  | 0 days?           | 20 days   | NA             | NA              | NA           | NA            | 0%       | Mon 4/6/18   | Sat 23/6/18  | 1472                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1474 | Third bay retaining wall   | 0 days?           | 20 days   | NA             | NA              | NA           | NA            | 0%       | Sun 24/6/18  | Fri 13/7/18  | 1473                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1475 | Mass concrete wall   | 0 days?           | 15 days   | NA             | NA              | NA           | NA            | 0%       | Sat 14/7/18  | Sat 28/7/18  | 1474                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1476 | Access Ramp and backfilling  | 20 days           | 20 days   | Sat 25/11/17   | Thu 14/12/17    | NA           | NA            | 0%       | Sun 29/7/18  | Fri 17/8/18  |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1477 | First Bay of Access Ramp   | 0 days?           | 7 days    | NA             | NA              | NA           | NA            | 0%       | Sun 29/7/18  | Sat 4/8/18   | 1468,1469,1475          |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1478 | Second Bay of Access Ramp  | 0 days?           | 7 days    | NA             | NA              | NA           | NA            | 0%       | Sun 5/8/18   | Sat 11/8/18  | 1477                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1479 | Backfilling  | 0 days?           | 6 days    | NA             | NA              | NA           | NA            | 0%       | Sun 12/8/18  | Fri 17/8/18  | 1478                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1480 | Rising main from Pumping Station to CBH 712 for future connection              | 20 days           | 20 days   | Sat 25/11/17   | Thu 14/12/17    | NA           | NA            | 0%       | Sun 29/7/18  | Fri 17/8/18  | 1476SS                  |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1481 | Connection of sewer drain from Pumping Station to Manhole 1807                 | 20 days           | 20 days   | Sun 17/12/17   | Fri 5/1/18      | NA           | NA            | 0%       | Sat 18/8/18  | Thu 6/9/18   | 1480                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1482 |  |                   |           |                |                 |              |               |          |              |              |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1483 | Plumbing Work & Drawpits for utilities   | 50 days           | 221 days  | Fri 15/12/17   | Fri 2/2/18      | NA           | NA            | 0%       | Sat 18/8/18  | Tue 26/3/19  |                         |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1484 | Water meter box  | 20 days           | 20 days   | Sun 17/12/17   | Fri 5/1/18      | NA           | NA            | 0%       | Sat 18/8/18  | Thu 6/9/18   | 1467,1476,1480,1481FS-2 |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1485 | CLP drawpits and cable ducts   | 20 days           | 20 days   | Fri 15/12/17   | Wed 3/1/18      | NA           | NA            | 0%       | Sat 18/8/18  | Thu 6/9/18   | 1476                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1486 | Lighting pits  | 20 days           | 20 days   | Fri 15/12/17   | Wed 3/1/18      | NA           | NA            | 0%       | Sat 18/8/18  | Thu 6/9/18   | 1476                    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |
| 1487 | Cabling and Installation of Transformer  | 28 days           | 28 days   | Sat 6/1/18     | Fri 2/2/18      | NA           | NA            | 0%       | Fri 7/9/18   | Thu 4/10/18  | 1484,1485,1486          |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |    |

Project: Rolling Programme (Nov 2017)  
Date: 28 Nov 2017  
EOT Entitlement Programme based on Master Programme (Rev 0-A)



Contract no. DC/2014/01  
Castle Peak Road Trunk Sewer and  
Tuen Mun Village Sewerage

| ID   | Task Name   | Baseline Duration | Duration  | Baseline Start | Baseline Finish | Actual Start | Actual Finish | % complete | Start        | Finish       | Predecessors                  | 15 | Q3 | Q4 | 2016 | Q1 | Q2 | Q3 | Q4 | 2017 | Q1 | Q2 | Q3 | Q4 | 2018 | Q1 | Q2 | Q3 | Q4 | 2019 | Q1 | Q2 | Q3 | Q4 | 2020 | Q1 | Q2 | Q3 | Q4 |  |  |
|------|---|-------------------|-----------|----------------|-----------------|--------------|---------------|------------|--------------|--------------|-------------------------------|----|----|----|------|----|----|----|----|------|----|----|----|----|------|----|----|----|----|------|----|----|----|----|------|----|----|----|----|--|--|
| 1488 | CLP energization  | 0 days            | 0 days    | Fri 2/2/18     | Fri 2/2/18      | NA           | NA            | 0%         | Tue 26/3/19  | Tue 26/3/19  | 1450,1487                     |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1489 |   |                   |           |                |                 |              |               |            |              |              |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1490 | Remaining works and Handing Over to E&M for Testing and Commissioning   | 120 days          | 120 days  | Thu 4/1/18     | Thu 3/5/18      | NA           | NA            | 0%         | Wed 5/9/18   | Wed 2/1/19   |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1491 | Recycle Timber plastic cladding of External Finishng of Pumping Station   | 60 days           | 60 days   | Thu 4/1/18     | Sun 4/3/18      | NA           | NA            | 0%         | Wed 5/9/18   | Sat 3/11/18  | 1452FS-30 days                |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1492 | Metal fence wall & Gate   | 60 days           | 60 days   | Thu 4/1/18     | Sun 4/3/18      | NA           | NA            | 0%         | Wed 5/9/18   | Sat 3/11/18  | 1453FS-30 days                |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1493 | Tempred glass fence on roof   | 30 days           | 30 days   | Sat 3/2/18     | Sun 4/3/18      | NA           | NA            | 0%         | Fri 5/10/18  | Sat 3/11/18  | 1491FS-30 days,1492FS-30 days |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1494 | Green Roof  | 45 days           | 45 days   | Mon 5/3/18     | Wed 18/4/18     | NA           | NA            | 0%         | Sun 4/11/18  | Tue 18/12/18 | 1493                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1495 | U-channel   | 50 days           | 50 days   | Tue 13/2/18    | Tue 3/4/18      | NA           | NA            | 0%         | Mon 15/10/18 | Mon 3/12/18  | 1492FS-20 days                |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1496 | Road pavement around Pumping Station  | 50 days           | 50 days   | Mon 5/3/18     | Mon 23/4/18     | NA           | NA            | 0%         | Sun 4/11/18  | Sun 23/12/18 | 1495FS-30 days                |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1497 | Landscaping work  | 60 days           | 60 days   | Mon 5/3/18     | Thu 3/5/18      | NA           | NA            | 0%         | Sun 4/11/18  | Wed 2/1/19   | 1496FS-50 days                |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1498 | Handing Over to E&M (1019 days after commencement of Pumping Station)   | 0 days            | 0 days    | Thu 3/5/18     | Thu 3/5/18      | NA           | NA            | 0%         | Wed 2/1/19   | Wed 2/1/19   | 1494FF,1497                   |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1499 | E&M Work  | 260 days          | 260 days  | Sat 3/2/18     | Sat 20/10/18    | NA           | NA            | 0%         | Wed 27/3/19  | Wed 11/12/19 |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1500 | Installation of E&M work  | 120 days          | 120 days  | Sat 3/2/18     | Sat 2/6/18      | NA           | NA            | 0%         | Wed 27/3/19  | Wed 24/7/19  | 1488                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1501 | Installation of E&M works & Testing and Commissioning   | 140 days          | 140 days  | Sun 3/6/18     | Sat 20/10/18    | NA           | NA            | 0%         | Thu 25/7/19  | Wed 11/12/19 | 1500                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1502 |   |                   |           |                |                 |              |               |            |              |              |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1503 | Completion Section 11B  | 0 days            | 0 days    | Sat 20/10/18   | Sat 20/10/18    | NA           | NA            | 0%         | Wed 11/12/19 | Wed 11/12/19 | 1498FF+172 days,1501          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1504 | Section 11B - Inclement Weather Granted (EOT Claim No. 3.18, up to 31 July 2017)                                      | 0 days?           | 59 days   | NA             | NA              | NA           | NA            | 0%         | Thu 12/12/19 | Sat 8/2/20   | 1503                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1505 |   |                   |           |                |                 |              |               |            |              |              |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1506 |   |                   |           |                |                 |              |               |            |              |              |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1507 | Duration of Section 10A - Siu Lam Psychiatric Centre Sewage Pumping Station   | 750 days          | 750 days  | Mon 20/7/15    | Mon 7/8/17      | Mon 20/7/15  | Mon 7/8/17    | 100%       | Mon 20/7/15  | Mon 7/8/17   |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1508 | Inclement Weather Granted (EOT Claim No. 3.18, up to 31 July 2017)  | 0 days?           | 45 days   | NA             | NA              | Tue 8/8/17   | Thu 21/9/17   | 100%       | Tue 8/8/17   | Thu 21/9/17  | 1507                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1509 | Additional Time for Completion  | 0 days?           | 50 days   | NA             | NA              | Fri 22/9/17  | Fri 10/11/17  | 100%       | Fri 22/9/17  | Fri 10/11/17 | 1508                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1510 | Completion  | 0 days?           | 0 days    | NA             | NA              | Fri 10/11/17 | Fri 10/11/17  | 100%       | Fri 10/11/17 | Fri 10/11/17 | 1509,1565FF                   |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1511 |   |                   |           |                |                 |              |               |            |              |              |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1512 | Section 10A - Siu Lam Psychiatric Centre Sewage Pumping Station   | 750 days          | 800 days? | Mon 20/7/15    | Mon 7/8/17      | Mon 20/7/15  | NA            | 98%        | Mon 20/7/15  | Tue 26/9/17  |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1513 | Portion 10 - Time Possession of Site  | 60 days           | 60 days   | Mon 20/7/15    | Thu 17/9/15     | Mon 20/7/15  | Thu 17/9/15   | 100%       | Mon 20/7/15  | Thu 17/9/15  |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1514 | Preparation Work  | 90 days           | 90 days   | Fri 18/9/15    | Wed 16/12/15    | Fri 18/9/15  | Wed 16/12/15  | 100%       | Fri 18/9/15  | Wed 16/12/15 |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1515 | Initial Survey  | 60 days           | 60 days   | Fri 18/9/15    | Mon 16/11/15    | Fri 18/9/15  | Mon 16/11/15  | 100%       | Fri 18/9/15  | Mon 16/11/15 | 1513                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1516 | Site clearance  | 30 days           | 30 days   | Tue 17/11/15   | Wed 16/12/15    | Tue 17/11/15 | Wed 16/12/15  | 100%       | Tue 17/11/15 | Wed 16/12/15 | 1515                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1517 |   |                   |           |                |                 |              |               |            |              |              |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1518 | EOT Claim 021 - Delay due to Change of Design at SLPC SPS   | 0 days?           | 80 days   | NA             | NA              | Sat 10/9/16  | Tue 29/11/16  | 100%       | Sat 10/9/16  | Tue 29/11/16 |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1519 | Works were suspended due to design change   | 0 days?           | 0 days    | NA             | NA              | Sat 10/9/16  | Sat 10/9/16   | 100%       | Sat 10/9/16  | Sat 10/9/16  |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1520 | Partially updated design information was reviewed by AECOM and provided   | 0 days?           | 80 days   | NA             | NA              | Sat 10/9/16  | Mon 28/11/16  | 100%       | Sat 10/9/16  | Mon 28/11/16 | 1519                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1521 | Works resumed   | 0 days?           | 0 days    | NA             | NA              | Tue 29/11/16 | Tue 29/11/16  | 100%       | Tue 29/11/16 | Tue 29/11/16 | 1520                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1522 |   |                   |           |                |                 |              |               |            |              |              |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1523 | EOT Claim 033 - Change of Design in Siu Lam Psychiatric Centre SPS  | 0 days?           | 167 days? | NA             | NA              | Tue 29/11/16 | Sun 14/5/17   | 100%       | Tue 29/11/16 | Sun 14/5/17  |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1524 | Additional cast-in socket for davit is requested to install under updated construction details                        | 0 days?           | 0 days    | NA             | NA              | Tue 29/11/16 | Tue 29/11/16  | 100%       | Tue 29/11/16 | Tue 29/11/16 | 1521                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1525 | Order, Fabrication and Delivery of socket   | 0 days?           | 42 days?  | NA             | NA              | Tue 29/11/16 | Mon 9/1/17    | 100%       | Tue 29/11/16 | Mon 9/1/17   | 1524                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1526 | Ready for installation  | 0 days?           | 0 days    | NA             | NA              | Tue 10/1/17  | Tue 10/1/17   | 100%       | Tue 10/1/17  | Tue 10/1/17  | 1525                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1527 | Installation of cast-in davit and modification of installed RC bars   | 0 days?           | 3 days    | NA             | NA              | Tue 10/1/17  | Thu 12/1/17   | 100%       | Tue 10/1/17  | Thu 12/1/17  | 1526                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1528 | Construct Rising main (CH 307 to CH 282) from Pump House in advance Koisk due to increase of depth of pumping station | 0 days?           | 55 days   | NA             | NA              | Wed 22/2/17  | Mon 17/4/17   | 100%       | Wed 22/2/17  | Mon 17/4/17  | 1539                          |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |
| 1529 | Confirm details of additional 45 degree bend by AECOM   | 0 days?           | 0 days    | NA             | NA              | Wed 1/3/17   | Wed 1/3/17    | 100%       | Wed 1/3/17   | Wed 1/3/17   |                               |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |      |    |    |    |    |  |  |

|   |  |  |  |  |   |  |  |
|---|--|--|--|--|---|--|--|
| Project: Rolling Programme (Nov 2017)<br>Date: 28 Nov 2017<br>EOT Entitlement Programme based on Master Programme (Rev 0-A) | Task<br>Task Progress<br>Critical Task<br>Critical Task Progress<br>Critical | Task<br>Task Progress<br>Critical Task<br>Critical Task Progress<br>Critical | Critical Split<br>Baseline<br>Milestone<br>Baseline Milestone<br>Summary | Rolled Up Task<br>Rolled Up Critical Task<br>Rolled Up Milestone<br>Baseline Summary<br>Rolled Up Baseline | Rolled Up Baseline Milestone<br>Rolled Up Progress<br>Split<br>Baseline Split<br>External Tasks | Project Summary<br>Group By Summary<br>Inactive Task<br>Inactive Milestone<br>Deadline | Project Summary<br>Group By Summary<br>Inactive Task<br>Inactive Milestone<br>Deadline |
|---|--|--|--|--|---|--|--|

## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---




### **Appendix B**

#### **Project Organization Chart**

# FUGRO TECHNICAL SERVICES LIMITED


Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

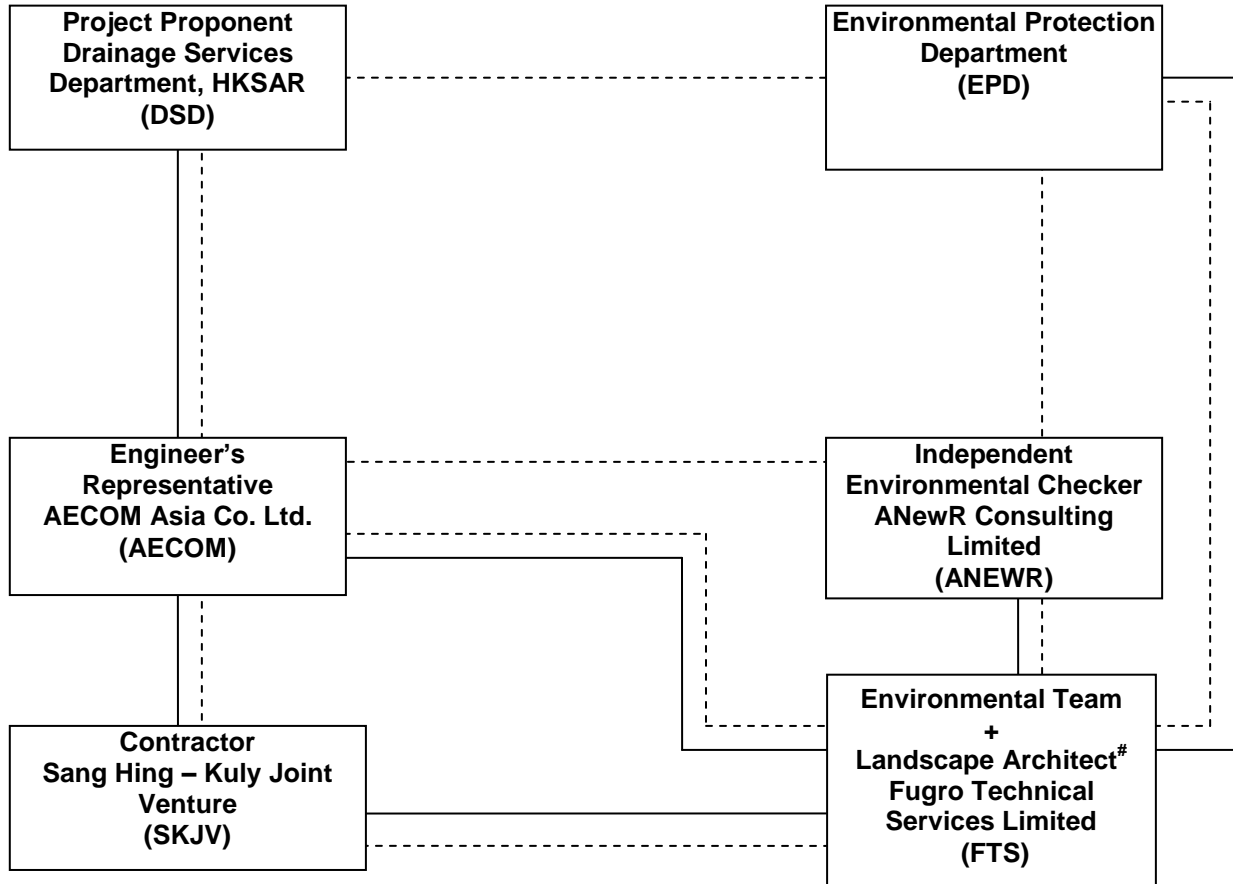

Remark:

# The Landscape Architect with a minimum of 1-2years on site experience as a member of the ET to monitor and audit the landscaping installation works and landscape protection measures.





## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Appendix C**

#### **Action and Limit Levels for Air Quality and Noise**

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



### Action and Limit Levels for Air Quality

| Parameter                             | Monitoring Station | Action Level ( $\mu\text{g}/\text{m}^3$ ) | Limit Level ( $\mu\text{g}/\text{m}^3$ ) |
|---------------------------------------|--------------------|---|--|
| 1-hr TSP ( $\mu\text{g}/\text{m}^3$ ) | LC6a               | 344                                       | 500                                      |
|                                       | LC9                | 335                                       |  |

### Action and Limit Levels for Construction Noise

| Time Period                      | Location    | Action                                    | Limit     |
|----------------------------------|-------------|---|-----------|
| 0700-1900 hrs on normal weekdays | LC6a<br>LC9 | When one documented complaint is received | 75* dB(A) |

\* reduce to 70 dB(A) for schools and 65 dB(A) during school examination periods.

## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Appendix D**

#### **Air Quality Monitoring Data and Graphical Presentations**

**FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.



Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

**LC6a The Castle Bay**

| 1-hour TSP ( $\mu\text{g}/\text{m}^3$ ) |            |        |        |        |         |
|---|------------|--------|--------|--------|---------|
| Date                                    | Start Time | 1st hr | 2nd hr | 3rd hr | Weather |
| 03-Aug-19                               | 08:50      | 63     | 63     | 73     | Cloudy  |
| 09-Aug-19                               | 09:20      | 39     | 43     | 48     | Fine    |
| 15-Aug-19                               | 08:49      | 57     | 49     | 66     | Fine    |
| 21-Aug-19                               | 14:02      | 54     | 56     | 42     | Fine    |
| 27-Aug-19                               | 09:09      | 54     | 50     | 51     | Fine    |
| 02-Sep-19                               | 13:00      | 48     | 55     | 44     | Fine    |
| 07-Sep-19                               | 13:03      | 54     | 50     | 62     | Fine    |
| 12-Sep-19                               | 08:40      | 61     | 53     | 68     | Fine    |
| 18-Sep-19                               | 08:23      | 40     | 54     | 38     | Fine    |
| 24-Sep-19                               | 08:50      | 59     | 71     | 63     | Fine    |
| 30-Sep-19                               | 08:50      | 63     | 63     | 73     | Fine    |
| 04-Oct-19                               | 08:31      | 63     | 68     | 55     | Fine    |
| 10-Oct-19                               | 09:15      | 73     | 71     | 68     | Fine    |
| 16-Oct-19                               | 08:50      | 43     | 34     | 39     | Fine    |
| 22-Oct-19                               | 09:13      | 62     | 58     | 62     | Fine    |
| 28-Oct-19                               | 09:05      | 113    | 116    | 182    | Fine    |
| 02-Nov-19                               | 08:40      | 69     | 63     | 69     | Fine    |
| 08-Nov-19                               | 08:30      | 60     | 64     | 57     | Fine    |
| 14-Nov-19                               | 14:00      | 113    | 105    | 90     | Cloudy  |
| 20-Nov-19                               | 14:00      | 73     | 71     | 39     | Fine    |
| 26-Nov-19                               | 14:30      | 128    | 114    | 135    | Fine    |

**LC9 Castle Peak Villas Block C**

| 1-hour TSP ( $\mu\text{g}/\text{m}^3$ ) |            |        |        |        |         |
|---|------------|--------|--------|--------|---------|
| Date                                    | Start Time | 1st hr | 2nd hr | 3rd hr | Weather |
| 03-Aug-19                               | 08:35      | 50     | 46     | 58     | Cloudy  |
| 09-Aug-19                               | 08:30      | 35     | 35     | 37     | Fine    |
| 15-Aug-19                               | 08:35      | 49     | 55     | 72     | Fine    |
| 21-Aug-19                               | 13:50      | 52     | 48     | 53     | Fine    |
| 27-Aug-19                               | 09:40      | 41     | 40     | 40     | Fine    |
| 02-Sep-19                               | 13:00      | 40     | 38     | 48     | Fine    |
| 07-Sep-19                               | 13:16      | 40     | 49     | 45     | Fine    |
| 12-Sep-19                               | 08:55      | 56     | 62     | 65     | Fine    |
| 18-Sep-19                               | 08:34      | 29     | 34     | 39     | Fine    |
| 24-Sep-19                               | 08:32      | 54     | 54     | 50     | Fine    |
| 30-Sep-19                               | 08:35      | 50     | 46     | 58     | Fine    |
| 04-Oct-19                               | 08:45      | 39     | 55     | 53     | Fine    |
| 10-Oct-19                               | 09:30      | 84     | 70     | 59     | Fine    |
| 16-Oct-19                               | 09:00      | 62     | 50     | 32     | Fine    |
| 22-Oct-19                               | 09:20      | 46     | 34     | 59     | Fine    |
| 28-Oct-19                               | 09:12      | 80     | 87     | 174    | Fine    |
| 02-Nov-19                               | 08:30      | 58     | 71     | 75     | Fine    |
| 08-Nov-19                               | 08:42      | 84     | 75     | 71     | Fine    |
| 14-Nov-19                               | 14:30      | 128    | 118    | 100    | Cloudy  |
| 20-Nov-19                               | 14:30      | 59     | 55     | 46     | Fine    |
| 26-Nov-19                               | 15:00      | 116    | 103    | 121    | Fine    |

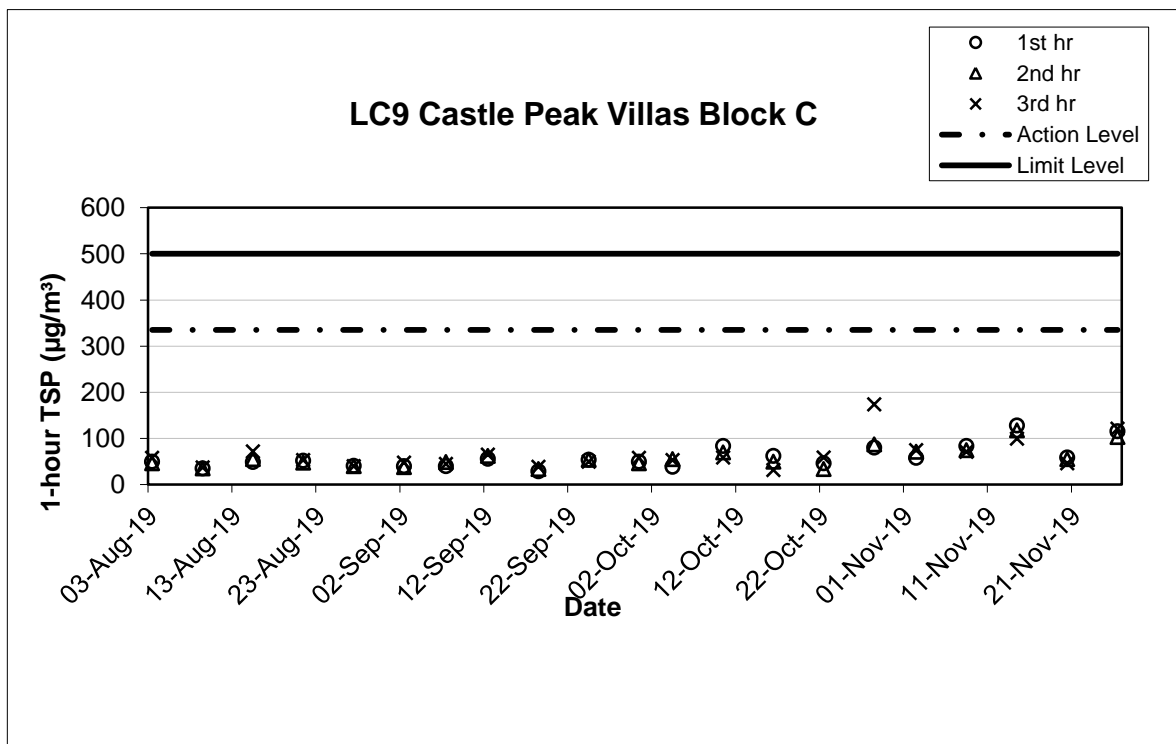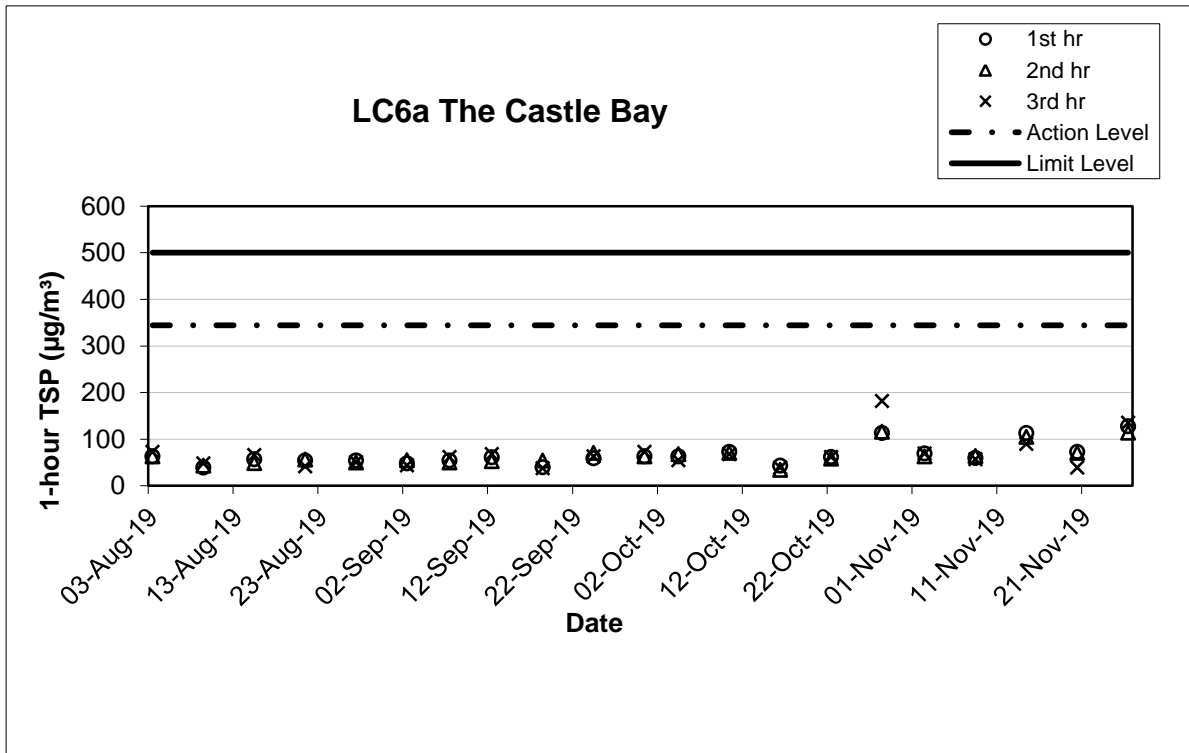

**Note:**

- 1) The major activities during the reporting period refer to section 1.4.1.
- 2) The weather conditions during the period refer to section 2.5.1.
- 3) The other factors influencing the monitoring results refer to section 2.6.

## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Appendix E**

#### **Noise Monitoring Data and Graphical Presentations**

**FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.



Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

**LC6a The Castle Bay**

| Date      | Start Time | L <sub>eq</sub> 30min dB(A) | Corrected Leq 30min dB(A) | L <sub>90</sub> dB(A) | L <sub>10</sub> dB(A) | Weather |
|-----------|------------|-----------------------------|---------------------------|-----------------------|-----------------------|---------|
| 03-Aug-19 | 08:55      | 70                          | 65                        | 67                    | 73                    | Cloudy  |
| 09-Aug-19 | 09:26      | 71                          | 66                        | 66                    | 74                    | Fine    |
| 15-Aug-19 | 09:28      | 67                          | 62                        | 63                    | 72                    | Fine    |
| 21-Aug-19 | 14:10      | 63                          | 58                        | 61                    | 65                    | Fine    |
| 27-Aug-19 | 09:05      | 73                          | 68                        | 69                    | 75                    | Fine    |
| 02-Sep-19 | 13:00      | 64                          | 59                        | 60                    | 68                    | Fine    |
| 07-Sep-19 | 14:01      | 64                          | 59                        | 60                    | 67                    | Fine    |
| 12-Sep-19 | 09:45      | 72                          | 67                        | 65                    | 73                    | Fine    |
| 18-Sep-19 | 08:49      | 69                          | 64                        | 69                    | 73                    | Fine    |
| 24-Sep-19 | 08:53      | 69                          | 64                        | 66                    | 73                    | Fine    |
| 30-Sep-19 | 08:55      | 70                          | 65                        | 67                    | 73                    | Fine    |
| 04-Oct-19 | 09:44      | 64                          | 59                        | 61                    | 66                    | Fine    |
| 10-Oct-19 | 09:13      | 69                          | 64                        | 66                    | 71                    | Fine    |
| 16-Oct-19 | 08:50      | 64                          | 59                        | 59                    | 67                    | Fine    |
| 22-Oct-19 | 09:11      | 64                          | 59                        | 58                    | 65                    | Fine    |
| 28-Oct-19 | 09:01      | 70                          | 65                        | 62                    | 73                    | Fine    |
| 02-Nov-19 | 08:45      | 67                          | 62                        | 63                    | 70                    | Fine    |
| 08-Nov-19 | 09:28      | 69                          | 64                        | 64                    | 73                    | Fine    |
| 14-Nov-19 | 14:00      | 69                          | 64                        | 58                    | 70                    | Cloudy  |
| 20-Nov-19 | 15:30      | 62                          | 57                        | 55                    | 63                    | Fine    |
| 26-Nov-19 | 14:30      | 61                          | 56                        | 51                    | 61                    | Fine    |

**LC9 Castle Peak Villas Block C**

| Date      | Start Time | L <sub>eq</sub> 30min dB(A) | Corrected Leq 30min dB(A) | L <sub>90</sub> dB(A) | L <sub>10</sub> dB(A) | Weather |
|-----------|------------|-----------------------------|---------------------------|-----------------------|-----------------------|---------|
| 03-Aug-19 | 09:45      | 67                          | N.A                       | 64                    | 71                    | Cloudy  |
| 09-Aug-19 | 08:32      | 68                          | N.A                       | 63                    | 69                    | Fine    |
| 15-Aug-19 | 08:32      | 62                          | N.A                       | 60                    | 68                    | Fine    |
| 21-Aug-19 | 14:52      | 59                          | N.A                       | 57                    | 61                    | Fine    |
| 27-Aug-19 | 09:43      | 67                          | N.A                       | 61                    | 69                    | Fine    |
| 02-Sep-19 | 13:40      | 58                          | N.A                       | 54                    | 61                    | Fine    |
| 07-Sep-19 | 13:14      | 58                          | N.A                       | 54                    | 60                    | Fine    |
| 12-Sep-19 | 09:00      | 72                          | N.A                       | 64                    | 75                    | Fine    |
| 18-Sep-19 | 09:41      | 68                          | N.A                       | 66                    | 73                    | Fine    |
| 24-Sep-19 | 09:50      | 67                          | N.A                       | 64                    | 69                    | Fine    |
| 30-Sep-19 | 09:45      | 67                          | N.A                       | 64                    | 71                    | Fine    |
| 04-Oct-19 | 08:51      | 58                          | N.A                       | 56                    | 61                    | Fine    |
| 10-Oct-19 | 09:59      | 63                          | N.A                       | 59                    | 64                    | Fine    |
| 16-Oct-19 | 09:34      | 65                          | N.A                       | 61                    | 68                    | Fine    |
| 22-Oct-19 | 09:53      | 51                          | N.A                       | 49                    | 53                    | Fine    |
| 28-Oct-19 | 09:42      | 52                          | N.A                       | 50                    | 54                    | Fine    |
| 02-Nov-19 | 09:30      | 66                          | N.A                       | 64                    | 68                    | Fine    |
| 08-Nov-19 | 08:45      | 66                          | N.A                       | 61                    | 70                    | Fine    |
| 14-Nov-19 | 15:00      | 51                          | N.A                       | 42                    | 53                    | Cloudy  |
| 20-Nov-19 | 16:10      | 60                          | N.A                       | 56                    | 63                    | Fine    |
| 26-Nov-19 | 15:20      | 67                          | N.A                       | 55                    | 60                    | Fine    |

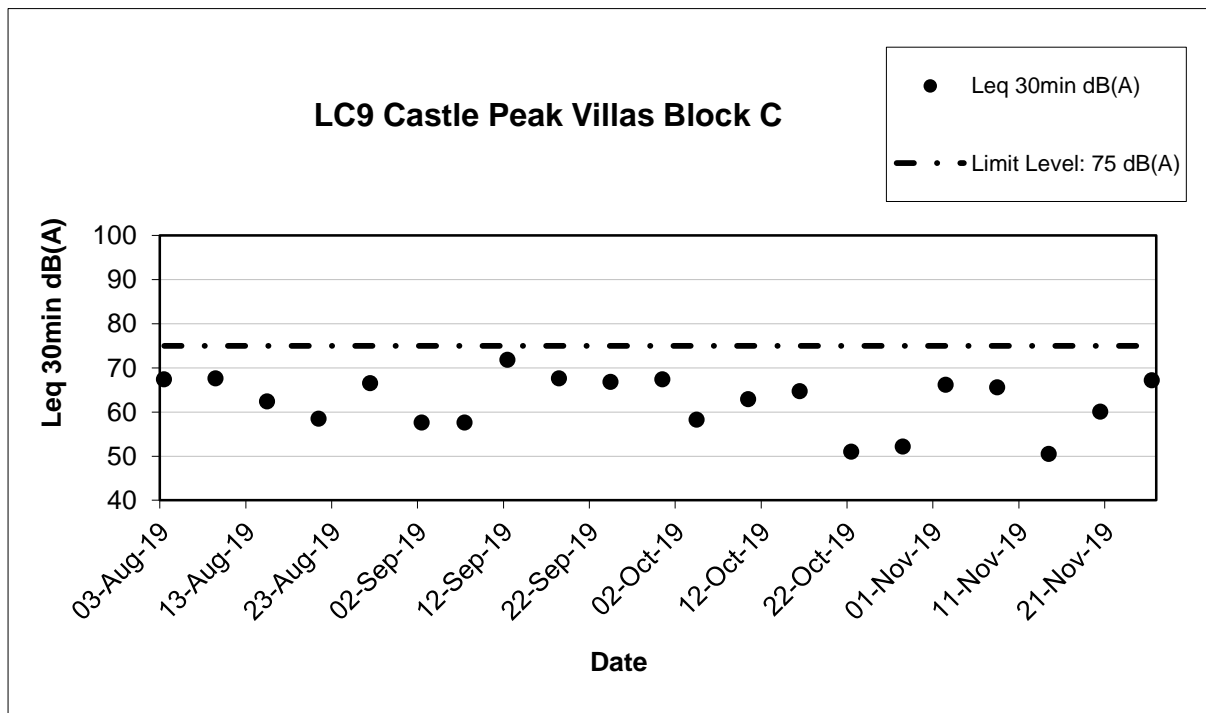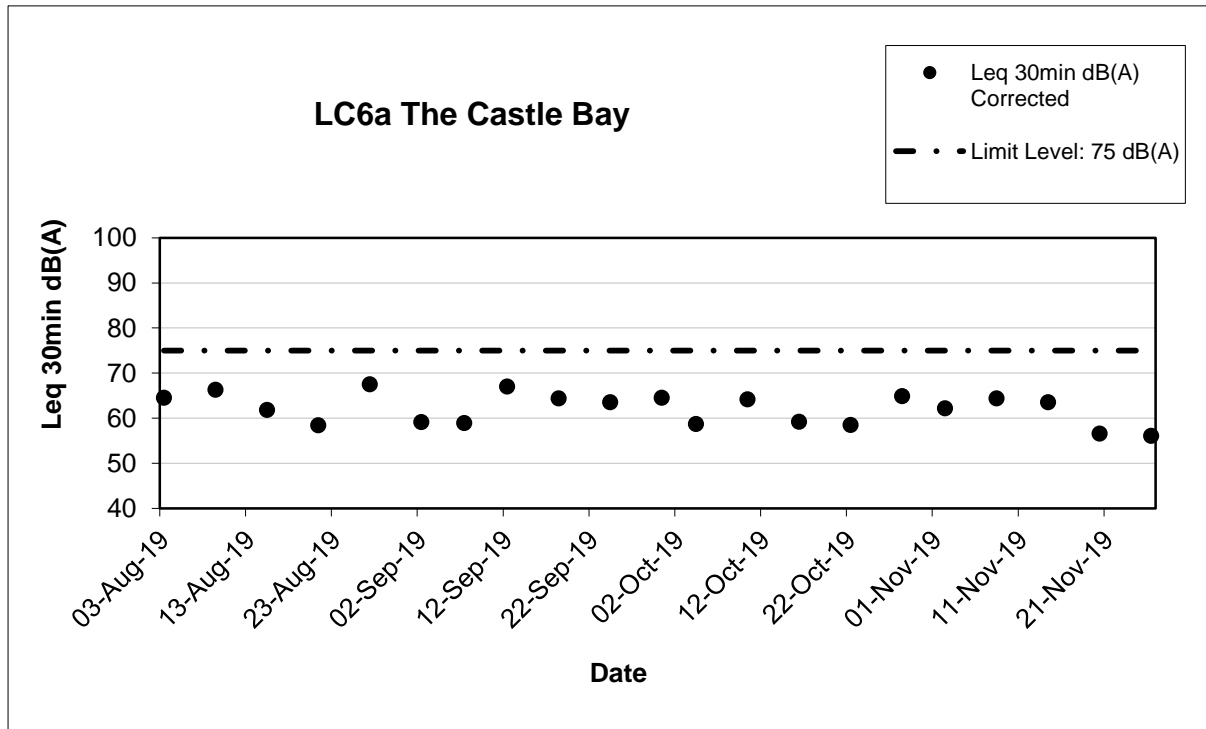

**Note:**

- 1) The major activities during the reporting period refer to section 1.4.1.
- 2) The weather conditions during the period refer to section 2.5.1.
- 3) The other factors influencing the monitoring results refer to section 2.6.



## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Appendix F**

#### **Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions**

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



### Environmental Complaints Log

| Complaint Log No. | Date of Receipt | Received From and Received By | Nature of Complaint | Date Investigated | Outcome | Date of Reply |
|-------------------|-----------------|-------------------------------|---------------------|-------------------|---------|---------------|
| Nil               | -               | -                             | -                   | -                 | -       | -             |

### Cumulative Statistics on Complaints

| Environmental Parameters | Cumulative No. Brought Forward | No. of Complaints This Month | Cumulative Project-to-Date |
|--------------------------|--------------------------------|------------------------------|----------------------------|
| Air                      | 0                              | 0                            | 0                          |
| Noise                    | 0                              | 0                            | 0                          |
| Water                    | 0                              | 0                            | 0                          |
| Waste                    | 0                              | 0                            | 0                          |
| Total                    | 0                              | 0                            | 0                          |

### Cumulative Statistics on Notifications of Summons and Successful Prosecutions

| Environmental Parameters | Cumulative No. Brought Forward | No. of Prosecutions This Month | Cumulative Project-to-Date |
|--------------------------|--------------------------------|--------------------------------|----------------------------|
| Air                      | 0                              | 0                              | 0                          |
| Noise                    | 0                              | 0                              | 0                          |
| Water                    | 0                              | 0                              | 0                          |
| Waste                    | 0                              | 0                              | 0                          |
| Total                    | 0                              | 0                              | 0                          |

## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Appendix G**

#### **Implementation Status of Environmental Mitigation Measures**

# FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



## Air Quality

| EIA Reference | Environmental Protection Measures   | Location/ Timing  | Implementation Agent | Relevant Standard or Requirement                | Implementation Status in Construction Phase |
|---------------|---|---|----------------------|---|---|
| 4.5           | Undertake all air pollution measures to prevent dust nuisance as a result of and during construction activities.                                      | All unpaved haul roads, bulldozed material, exposed site areas / Throughout construction period | Contractor           | TMEIA   | ^   |
| 4.5           | No debris or other materials shall be burnt on the works areas.   | All areas / Throughout construction period  | Contractor           | TMEIA.<br>Avoid smoke impacts and disturbance   | ^   |
| 4.5           | Dust suppression measures shall be provided and to be submitted to and approved by the Engineer.  | All areas / Throughout construction period  | Contractor           | TMEIA   | ^   |
| 4.5           | Stockpiles of imported material kept on site shall be contained within hoardings, dampened and/or covered during dry and windy weather.               | All areas / Throughout construction period  | Contractor           | TMEIA<br>Avoid dust generation                  | ^   |
| 4.5           | Material stockpiled along side trenches should be covered with tarpaulins whenever works are within village boundaries.                               | All areas / Throughout construction period  | Contractor           | TMEIA<br>Avoid dust generation / visual impacts | ^   |
| 4.5           | Water sprays shall be used during the delivery and handling of cement, sands aggregates and the like.   | All areas / Throughout construction period  | Contractor           | TMEIA<br>Avoid dust generation                  | ^   |
| 4.5           | No batching of concrete should be carried out on site. Concrete should be used in ready mixed form and off loaded adjacent to designated works areas. | All areas / Throughout construction period  | Contractor           | TMEIA   | ^   |

# FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



| EIA Reference | Environmental Protection Measures   | Location/ Timing   | Implementation Agent | Relevant Standard or Requirement          | Implementation Status in Construction Phase |
|---------------|---|--|----------------------|---|---|
| 4.5           | Any vehicle used for moving cement, sands, aggregates and construction waste and the like shall have properly fitting side and tail boards. Materials shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards. | All areas / Throughout construction period                                     | Contractor           | TMEIA Avoid dust and spillage of material | ^   |
| 4.5           | No earth, mud, debris, dust and the like shall be deposited on public roads. Details of proposals for the wheel cleaning facilities shall be agreed with the Engineer. Such wheel washing facility shall be usable prior to any earthworks excavation activity on the Site.   | All areas, particularly pumping station sites / Throughout construction period | Contractor           | TMEIA Avoid spread/ deposition of mud     | ^   |
| 4.6.9         | Pumping station vent shafts should be located away from sensitive receivers.  | All pumping stations   | DSD                  | TMEIA Avoid odour impacts                 | N/A   |
| 4.6.18        | Use a covered container to store and transport the screenings from the pump house.  | All pumping stations /operational phase  | DSD                  | TMEIA Avoid odour impacts                 | N/A   |
| 4.6.18        | Undertake the collection of the screenings and transfer to the covered container within the confines of the pump house.   | All pumping stations / operational phase                                       | DSD                  | TMEIA Avoid odour impacts                 | N/A   |
| 11.2.8        | EM&A in the form of 1 hour total suspended particulates monitoring once per week  | All sensitive representative receivers / Throughout construction period        | Contractor           | EM&A Manual                               | ^   |

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



### Noise

| EIA Reference | Environmental Protection Measures   | Location/ Timing  | Implementation Agent | Relevant Standard or Requirement | Implementation Status in Construction Phase |
|---------------|---|---|----------------------|----------------------------------|---|
| 5.7.1 & 5.8.1 | Ensure silencers are installed on the exhaust pipes of the trucks, excavators, compactors, concrete lorry mixer, and cranes for all activities.   | All areas / Throughout construction period  | Contractor           | TMEIA                            | ^   |
| 5.7.1 & 5.8.1 | Use of mufflers on the breakers for all activities.   | All areas / Throughout construction period  | Contractor           | TMEIA                            | N/A   |
| 5.7.1 & 5.8.1 | Use of temporary noise barriers for all activities at the pumping station sites and during main sewer construction. During main sewer construction, barriers should be used to screen the activities of mobile equipment including the crane and excavator. | All pumping stations and main sewer construction locations / Throughout construction period | Contractor           | TMEIA                            | N/A   |
| 5.5.10        | Use of temporary noise barriers for all activities in the villages, where there is at least a 5m clearance  | Village sewer alignment / Throughout construction period                                    | Contractor           | TMEIA                            | ^   |
| 5.8.6 & 5.9.6 | Manual breaking of concrete, where the concrete is less than 50mm thick.  | Sewer alignment construction / concrete breaking activities                                 | Contractor           | TMEIA                            | N/A   |
| 5.8.6 & 5.9.6 | Use of alternative pavement removal methods/equipment (kick ripper), where the concrete is less than 100mm thick  | Sewer alignment construction / concrete breaking activities                                 | Contractor           | TMEIA                            | N/A   |

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



| EIA Reference | Environmental Protection Measures  | Location/ Timing  | Implementation Agent | Relevant Standard or Requirement | Implementation Status in Construction Phase |
|---------------|--|---|----------------------|----------------------------------|---|
| 5.8.6 & 5.9.6 | Use of acoustic enclosure in place of a barrier where there is a 6m clearance.   | Sewer alignment construction / Throughout construction period | Contractor           | TMEIA                            | N/A   |
| 5.8.6 & 5.9.6 | Scheduling the numbers and operating times of equipment, when noise levels cannot be reduced to within the standards by other means        | Sewer alignment construction / Throughout construction period | Contractor           | TMEIA                            | ^   |
| 5.8.11        | The construction activities should be carried out in the daytime period (08.00- 18.00) only and shall exclude Sundays and public holidays. | All areas   | Contractor           | TMEIA                            | ^   |
| 5.8.11        | Powered mechanical equipment shall not be used within 5m of an NSR without the permission of the Engineer                                  | All areas / Throughout construction period                    | Contractor           | TMEIA                            | ^   |
| 5.8.11        | Carry out good site practice to limit noise emission at source.  | All areas / Throughout construction period                    | Contractor           | TMEIA                            | ^   |
| 5.8.11        | Avoid simultaneous noisy activities.   | All areas / Throughout construction period                    | Contractor           | TMEIA                            | ^   |
| 11.2.8        | EM&A in the form of noise monitoring.  | All representative receivers / Throughout construction period | Contractor           | EM&A Manual                      | ^   |

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



### Water Quality

| EIA Reference | Environmental Protection Measures   | Location/ Timing                           | Implementation Agent | Relevant Standard or Requirement | Implementation Status in Construction Phase |
|---------------|---|--|----------------------|----------------------------------|---|
| 6.4.3         | Stockpiles of excavated material should be kept to a minimum and covered during times of heavy rainfall.  | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.4.10        | Pass any trench dewatering through a portable sand/silt removal traps prior to discharge.   | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.5.2         | When works are carried out during the rainy season exposed slopes, stockpiles should be covered with tarpaulin and temporary access roads protected with a layer of gravel or crushed stone.                    | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | N/A   |
| 6.5.2         | Surface run off should be discharged to storm drains via sand/silt removal traps.   | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.5.2         | Channels, bunds or sand bags should be used to direct any storm water to the traps and perimeter channels should be constructed before the main works begin to prevent external run off from crossing the site. | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.5.2         | Silt removal structures, channels and manholes should be maintained to remove accumulated material, specifically at the onset and end of rainy periods.   | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |



## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



| EIA Reference | Environmental Protection Measures  | Location/ Timing                           | Implementation Agent | Relevant Standard or Requirement  | Implementation Status in Construction Phase |
|---------------|--|--|----------------------|---|---|
| 6.5.2         | Trenches for the sewer main should be dug and backfilled in short sections to minimise the quantities of rain water which will need to be pumped from them and upslope bunding provided to prevent surface water from flowing into the trenches. | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94   | N/A   |
| 6.5.2         | Rainwater pumped from the trenches should be discharged to storm drains via sand/silt removal traps.   | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94   | N/A   |
| 6.5.2         | Discharges to natural water courses should only take place when the effluent can be shown to comply with the relevant specified standards.   | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94 & Technical Memorandum on Standards for Effluent Discharged in Drainage and Sewerage Systems, Inland and Coastal Waters | ^   |
| 6.5.3         | All plant should be in proper working order and maintained such that there is no leakage of fuel or oil. Any waste oils should be collected in designated tanks prior to disposal off site.  | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94   | ^   |
| 6.5.3         | All mechanical plant maintenance and refuelling areas shall be sited on paved areas. All storm water run-off from these areas should be discharged via oil separators/petrol separators and sand/silt removal traps.                             | All areas / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94   | ^   |

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



| EIA Reference | Environmental Protection Measures   | Location/ Timing  | Implementation Agent | Relevant Standard or Requirement | Implementation Status in Construction Phase |
|---------------|---|---|----------------------|----------------------------------|---|
| 6.5.4         | Groundwater pumped out of excavations for the construction of pump sumps should only be discharged following removal of silt by sand/silt removal traps.  | All areas / throughout construction period                                    | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.5.5         | Water from drilling of rock should be discharged following removal of silt by sand/silt removal traps.  | All areas / throughout construction period                                    | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.5.6         | The wheels of all vehicles leaving the construction site should be washed before leaving the site to minimise the carry over of mud onto public roads. Wheel wash water should be recycled and only discharged following removal of silt by sand/silt removal traps.  | All areas particularly pumping station sites / throughout construction period | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.5.7         | Run off from the roofs of site buildings should be conveyed in closed drains to the nearest surface water course to prevent the generation of excessive quantities of surface water run off carrying suspended solids.  | Site Office areas / throughout construction period                            | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.5.7         | All spillages should be cleaned up immediately to prevent their downward migration into the groundwater.  | All areas / throughout construction period                                    | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |
| 6.5.7         | Sewage from toilets and any kitchens in the site facilities should be treated via a septic tank system or if this is not practicable chemical toilets should be provided and the waste from these together with 'grey water' removed from the site on a daily basis for disposal at an appropriate receiving point. | All areas / throughout construction period                                    | Contractor           | WPCO, TMEIA & ProPECC PN 1/94    | ^   |

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



| EIA Reference | Environmental Protection Measures  | Location/ Timing                          | Implementation Agent | Relevant Standard or Requirement | Implementation Status in Construction Phase |
|---------------|--|---|----------------------|----------------------------------|---|
| 6.6.2         | Overflow bypasses to be used in emergency situations only and no effluent should be discharged during regular maintenance. | All pumping stations / Operation          | DSD                  | WPCO, TMEIA                      | N/A   |
| 6.6.3 & 6.6.4 | Supply pumping stations with stand-by pumps, emergency power supplies and telemetry system.                                | All Pumping Stations                      | DSD                  | WPCO, TMEIA & ProPECC PN 1/94    | N/A   |
| 11.2.8        | EM&A in the form of site supervision to ensure water quality protection measures are implemented.                          | All areas/ Throughout construction period | Contractor           | EM&A                             | ^   |

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



### Waste Management

| EIA Reference | Environmental Protection Measures   | Location/ Timing  | Implementation Agent | Relevant Standard or Requirement  | Implementation Status in Construction Phase |
|---------------|---|---|----------------------|---|---|
| 7.12.1        | The Contractor shall identify a coordinator for the management of waste. The coordinator shall prepare a Waste Management Plan which specifies procedures such as a ticketing system, to facilitate tracking of loads and to ensure that illegal disposal of wastes does not occur, and protocols for the maintenance of records of the quantities of wastes generated, recycled and disposed. The Waste Management Plan shall be prepared with reference to Works Branch Technical Circular (WBTC) No. 5/99 for the Trip-ticket System for Disposal of Construction and Demolition Material and issued to the DEP and CED to confirm the availability for C&D and public fill waste. | Plan to be prepared prior to the start of construction, Implementation throughout construction period / All areas | Contractor           | TMEIA.Works Branch Technical Circular (WBTC) No. 5/99 for the Trip-ticket System for Disposal of Construction and Demolition Material | ^   |
| 7.12.1        | Stockpiled material should avoid vegetated areas where possible and covered by tarpaulins. Storage of material on site should be kept to a minimum.   | All areas/ Throughout construction period   | Contractor           | TMEIA. Prevent windblown dust and/or surface run-off / avoid nuisance to local residents  | ^   |
| 7.12.1        | Surplus material should be sorted on site into C&D waste and that suitable for public fill  | All areas /throughout construction period   | Contractor           | TMEIA. Maximise reusable material   | ^   |
| 7.12.1        | The contractor should provide a temporary storage area for general refuse during the construction phase which should be enclosed to avoid refuse being windblown and affected by rain. General refuse should be stored on site for a minimum period and disposed of at a licenced facility.   | All areas / throughout construction period  | Contractor           | TMEIA   | ^   |

## FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



| EIA Reference | Environmental Protection Measures  | Location/ Timing                           | Implementation Agent | Relevant Standard or Requirement  | Implementation Status in Construction Phase |
|---------------|--|--|----------------------|---|---|
| 7.12.1        | Excavated material in trucks shall be covered by tarpaulins to reduce the potential for spillage.  | All areas / throughout construction period | Contractor           | TMEIA   | ^   |
| 7.12.1        | Suitable chemical waste storage areas shall be formed on the site for temporary storage pending collection. All chemical wastes shall be handled, stored, transported and disposed of in accordance with the relevant practices. | All areas / throughout construction period | Contractor           | TMEIA/ Code of Practice on the Package, Labelling and Storage of Chemical Wastes and A Guide to the Chemical Waste Control Scheme | ^   |
| 7.12.1        | Nightsoil arising from chemical toilets and on site chemical treatment facilities shall be transported by a licensed contractor to government Sewage Treatment Works for disposal.   | All areas / throughout construction period | Contractor           | TMEIA/ Sanitation and Conservancy (Regional Council) By-laws  | ^   |
| 7.12.1        | Any screenings and grit that are removed during maintenance shall be disposed of at a landfill site. The material shall be suitably contained and covered.   | All areas / operational phase              | DSD                  | TMEIA   | N/A   |
| 11.2.8        | EM&A in the form of supervision of waste management practices  | All areas / throughout construction period | Contractor           | EM&A  | ^   |

# FUGRO TECHNICAL SERVICES LIMITED

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com



## Landscape and Visual

| EIA Reference  | Environmental Protection Measures   | Location/ Timing  | Implementation Agent | Relevant Standard or Requirement            | Implementation Status in Construction Phase |
|--|---|---|----------------------|---|---|
| 10.8.5,<br>10.9.15,<br>10.10.6,<br>10.10.11,<br>10.10.20,<br>10.11.6 | Use of a suitable colour scheme to the pump station building to match the design of the adjacent properties.  | All pumping stations  | DSD & Contractor     | Reduce visual intrusion of pumping stations | N/A   |
| 10.8.5,<br>10.9.15,<br>10.10.11,<br>10.10.20,<br>10.11.6             | Construction of boundary wall similar to the adjacent housing instead of standard chain link and barbed wire fence.   | All pumping stations except Tai Lam Correctional Institution  | DSD & Contractor     | Screen pumping stations                     | N/A   |
| 10.8.5,<br>10.9.15,<br>10.10.11,<br>10.10.20,<br>10.11.6             | Planting of trees and shrubs to the boundary of the pumping station compound.   | All pumping stations except Tai Lam Correctional Institution  | DSD & Contractor     | Screen pumping stations                     | N/A   |
| 10.8.6   | Minimise damage to the rootball of the tree east of the pumping station site.   | East of Castle Peak Villas pumping station/ During excavation | DSD and Contractor   |   | ^   |
| 11.2.8   | EM&A in the form of site supervision of protection measures for trees and landscaping and compensatory planting establishment during the construction and operational phases respectively | All areas   | Contractor           | EM&A  | ^   |

Remarks: ^

Compliance of mitigation measure

\*

Recommendation was made during site audit but improved/ rectified by the Contractor

N/A

Not Applicable at this stage as no such site activities were conducted in the reporting month

## **FUGRO TECHNICAL SERVICES LIMITED**

Fugro Development Centre,  
5 Lok Yi Street, Tai Lam,  
Tuen Mun, N.T.,  
Hong Kong.

Tel : +852 2450 8233  
Fax : +852 2450 6138  
E-mail : matlab@fugro.com  
Website : www.fugro.com

---



### **Appendix H**

#### **Monthly Summary of Waste Flow Table**





**Sang Hing – Kuly Joint Venture**  
**Environmental Monthly Report for Contract No. DC/2014/01**  
**Castle Peak Road Trunk Sewer and Tuen Mun Village Sewage**

Name of Department: DSD

Contract No.: DC/2014/01

| Forecast of Total Quantities of C&D Materials to be Generated from the Contract* |   |  |  |   |   |                        |   |                                      |                               |   |
|--|---|--|--|---|---|------------------------|---|--------------------------------------|-------------------------------|---|
| Total Quantity Generated<br>(in '000m <sup>3</sup> )                             | Hard Rock and Large Broken Concrete<br>(in '000m <sup>3</sup> ) | Reused in the Contract<br>(in '000m <sup>3</sup> ) | Reused in other Projects<br>(in '000m <sup>3</sup> ) | Disposed as Public Fill<br>(in '000m <sup>3</sup> ) | Imported Fill<br>(in '000m <sup>3</sup> ) | Metals<br>(in '000 kg) | Paper/ cardboard packaging<br>(in '000kg) | Plastics (see Note 3)<br>(in '000kg) | Chemical Waste<br>(in '000kg) | Others, e.g. general refuse<br>(in '000m <sup>3</sup> ) |
| 27   | 10  | 8  | 1  | 1   | 0   | 2                      | 1   | 1                                    | 1                             | 2   |

Notes:

- (1) The performance targets are given in ETWB Technical Circular PS Clause 6(14).
- (2) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material
- (4) \*The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m<sup>3</sup>. (ETWB Technical Circular PS Clause 5(4)(b) refers).  
 [Delete Note (4) and the table above on the forecast, where inapplicable].
