#### QUARTERLY EM&A REPORT

The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: 24<sup>th</sup> Quarterly EM&A Report (1 August 2017 to 31 October 2017)

Issue Date: February 2018

**Environmental Resources Management** 

16/F Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

#### QUARTERLY EM&A REPORT

The Jockey Club CPS Limited

# Central Police Station Conservation and Revitalisation Project: 24<sup>th</sup> Quarterly EM&A Report (1 August 2017 to 31 October 2017)

Issue Date: February 2018

Reference 0095646

For and on behalf of ERM-Hong Kong, Limited			
Approved by:	Frank Wan		
	Warderth J.		
Signed:	7		
Position: Partner			
Certified by: (Environmental Team Leader – Katie Yu)			
Date:	5 February 2018		

This report has been prepared by ERM-Hong Kong, Limited with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client.

We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.

This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.



香港九龍尖沙咀海港城 九倉電訊中心十三樓 13/F Wharf T&T Centre Harbour City Tsim Sha Tsui Kowloon Hong Kong

**電話 Tel (852) 2972 1000** 傳真 Fax (852) 2890 6343

info.hk@atkinsglobal.com www.atkinsglobal.com

Your ref. 0095646\_let\_Atkins\_20180207 Quarterly EM&A Report No.24.doc Our ref. 5121189/17.20/OC133/KC/EK

Date: 8 February 2018

#### By Post and Email (katie.yu@erm.com)

ERM-Hong Kong Limited, 16/F Berkshire House, 25 Westlands Road, Quarry Bay, Hong Kong

Attn: Ms Katie Yu

Dear Katie,

#### Central Police Station Conservation and Revitalization Project Verification of Quarterly EM&A Report No. 24

We refer to your letter dated 7 February 2018 regarding the Quarterly EM&A Report No. 24. Atkins China Limited verifies, in the capacity of Independent Environmental Checker, that the report conforms the requirements provided in Section 10.4 of the EM&A Manual.

Yours sincerely, For Atkins China Limited

ett

Keith Chau Independent Environmental Checker

c.c. HKJC – Mr. Kenneth Lee (By Email) Rocco Design Architect – Mr. Charles Kung (By Email)

	EXECUTIVE SUMMARY	Ι
1	INTRODUCTION	1
1.1	Purpose of the Report	1
1.2	STRUCTURE OF THE REPORT	1
2	PROJECT INFORMATION	3
2.1	BACKGROUND	3
2.2	SITE DESCRIPTION	3
2.3	CONSTRUCTION ACTIVITIES	3
2.4	CONSTRUCTION PROGRAMME	4
2.5	PROJECT ORGANISATION AND MANAGEMENT STRUCTURE	4
2.6	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	4
3	ENVIRONMENTAL MONITORING REQUIREMENTS	6
3.1	Noise Monitoring	6
3.2	Cultural Heritage	8
3.3	LANDSCAPE AND VISUAL MONITORING	9
3.4	ENVIRONMENTAL REQUIREMENTS IN CONTRACT DOCUMENTS	9
4	IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES	10
5	MONITORING RESULTS	11
5.1	Noise	11
5.2	LANDSCAPE AND VISUAL MONITORING	11
5.3	Cultural Heritage	13
5.4	WASTE MANAGEMENT	16
5.5	EFFECTIVENESS OF MITIGATION MEASURES AND MONITORING	16
6	ENVIRONMENTAL SITE INSPECTION	17
7	ENVIRONMENTAL NON-CONFORMANCE	19
8	<b>REVIEW OF THE EM&amp;A DATA AND EIA PREDICTIONS</b>	21
8.1	NOISE	21
8.2	WASTE MANAGEMENT	21
8.3	SUMMARY OF REVIEW	22
9	CONCLUSIONS	23

### LIST OF TABLES

- Table 2.1
   Summary of Construction Activities undertaken in this Reporting Period
- Table 2.2
   Summary of Environmental Licensing, Notification and Permit Status
- Table 3.1Construction Phase Noise Monitoring Locations
- Table 3.2Noise Monitoring Equipment
- Table 3.3Action and Limit Levels for Construction Noise Monitoring
- Table 3.4Alert, Alarm and Action (AAA) Levels for Vibration Monitoring
- Table 3.5Event and Action Plan for vibration monitoring
- Table 4.1Status of Required Submissions
- Table 5.1Findings of Monthly Tree Inspection in the Reporting Period
- Table 5.2Quantities of Waste Generated from the Project
- Table 8.1Comparison of Construction Noise Standard and Noise Monitoring Results
- Table 8.2Quantity of Actual Amount of C&D Materials, General Wastes and ChemicalWastes Generated and EIA Estimation

### LIST OF ANNEXES

- Annex A Locations of Works Areas and the Surroundings
- Annex A1 Project Location
- Annex A2 Declared Monuments within the Project Site
- Annex A3 Site Layout Plan marked with Works
- Annex B Project Organization Chart and Contact Detail
- Annex C Locations of Noise Monitoring Stations and Noise Sensitive Receivers
- Annex D Monitoring Schedule of the Reporting Period
- Annex E Calibration Reports for Calibrators and Sound Level Meters
- Annex F Event/Action Plans for Noise
- Annex G Summary of Implementation Status
- Annex H Noise Monitoring Results
- Annex I Construction Programme of the Project
- Annex J Waste Flow Table
- Annex K Environmental Complaint/Enquiry, Environmental Summons and Prosecution Log
- Annex L Records of Vibration Monitoring for Other Construction Works
- Annex M Summary of Condition of Character Defining Elements, Historic Buildings and Structures

### EXECUTIVE SUMMARY

The construction works of **Central Police Station Conservation and Revitalisation Project** commenced on 24 October 2011. This is the 24<sup>th</sup> quarterly Environmental Monitoring and Audit (EM&A) summary report presenting the EM&A works carried out during the period from 1 August 2017 to 31 October 2017 in accordance with the EM&A Manual.

### Environmental Monitoring and Audit Progress

A summary of the monitoring activities undertaken in this reporting period is listed below:

•	Construction Noise Monitoring during normal weekdays at	
	each monitoring station	17 times
•	Joint Environmental Site Inspection	3 times
•	Heritage Site Inspection	75 times
•	Landscape & Visual Monitoring / tree inspection (1)	3 times
•	Vibration monitoring for other construction works	75 times

#### Noise

17 sets of 30-minute construction noise measurements were carried out at each of the monitoring stations (NM2 and NM6) during normal weekdays of the reporting period.

No exceedance of the Action or Limit Level of construction noise was recorded during the reporting period.

#### Cultural Heritage

No vibration monitoring was carried out for demolition works, trial piling or pile/bored piling works as the aforementioned works were not conducted during the reporting period.

#### Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

• 75 vibration monitoring measurements for the structural addition and alteration works at Block 11.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

75 heritage site inspections were conducted and the Contractor has generally implemented the necessary protection measures as recommended.

(1) An ad-hoc joint tree inspection for Tree 6 and Tree 7 was carried out during the reporting period.

### Landscape & Visual

Landscape and visual monitoring has commenced since October 2011 on a monthly basis. Three monthly tree inspections have been conducted by the arborist during the reporting period. An ad-hoc joint tree inspection for Tree 6 and Tree 7 was carried out by the representatives of the arborist, Contractor, IEC, ET, HKJC, EPD and relevant parties on 8 August 2017. The recommended actions have been performed by the Contractor as advised in the reporting period.

### Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. 382.24 tonnes of inert C&D materials and 170.55 tonnes of non-inert C&D materials were generated during the reporting period. No metal, paper/cardboard or plastics waste was recycled during the reporting period. No chemical waste was collected by licenced chemical waste collector during the reporting period.

### Environmental Site Inspection

Three joint environmental site inspections were carried out by the representatives of the Contractor, the IEC and the ET during the reporting period. Key observations and recommendations identified during the monthly site inspections were rectified by the Contractor in the subsequent monthly site inspections.

### Environmental Exceedance/Non-conformance/Compliant/Enquiry/ Summons and Prosecution

No exceedance of the Action or Limit Level of construction noise was recorded at designated monitoring stations during the reporting period.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

An enquiry was recorded regarding a published article on 31 July 2017 and a follow-up article on 5 August 2017 by Ming Pao. An investigation has been carried out to address the Ming Pao reports during the reporting period. The recommended follow-up actions are being implemented.

No environmental non-compliance event was recorded during the reporting period. No non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period.

No complaint was received during the reporting period.

No summons/prosecution was received in this reporting period.

### 1 INTRODUCTION

ERM-Hong Kong, Limited (ERM) was appointed by the Jockey Club CPS Limited (the CPS Ltd) as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the **Central Police Station Conservation and Revitalisation Project** (the Project).

### 1.1 PURPOSE OF THE REPORT

This is the 24<sup>th</sup> quarterly EM&A summary report, which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from 1 August 2017 and 31 October 2017.

### **1.2** STRUCTURE OF THE REPORT

The structure of the report is as follows:

Section 1: In	troduction
---------------	------------

details the scope and structure of the report.

### Section 2: Project Information

summarises background and scope of the Project, site description, project organization and contract details, construction programme, the construction works undertaken and the status of Environmental Permit(s)/License(s) during the reporting period.

#### Section 3: Environmental Monitoring Requirements

summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event/Action Plans, environmental mitigation measures as recommended in the EIA report, and relevant environmental requirements.

- Section 4 : **Implementation Status on Environmental Mitigation Measures** summarises the implementation of environmental protection measures during the reporting period.
- Section 5 : **Monitoring Results** summarises the monitoring and waste management results obtained in the reporting period.

### Section 6 : **Environmental Site Inspection** summarises the audit findings of the monthly site inspections undertaken within the reporting period.

#### Section 7: Environmental Non-conformance

summarises any monitoring exceedance, environmental complaints and environmental summons received within the reporting period.

## Section 8 : Review of the EM&A Data and EIA Predictions

compares the monitoring data and waste quantity against predictions in the approved Project EIA report.

Section 9: Conclusions

#### 2 PROJECT INFORMATION

#### 2.1 BACKGROUND

The Chief Executive (CE)'s 2007-2008 Policy Address highlighted revitalisation as the guiding principle of heritage conservation and the Project was among one of the specific proposals put forward by the CE in the same Policy Address. At the meeting of the Executive Council (ExCo) on 15 July 2008, the ExCo advised and the CE ordered that Government should enter into a partnership with the Hong Kong Jockey Club (HKJC) in the form of an agreement (or agreements) to take forward the conservation and revitalisation of the CPS project based on various guiding parameters. The Project is now being undertaken in partnership with the Development Bureau of the HKSAR Government. The HKJC has taken on board the decision at the ExCo meeting and further investigated the design and implementation of the Project. The Project is now implemented by the Jockey Club CPS Limited.

#### 2.2 SITE DESCRIPTION

The location of the Project Site is shown in *Annex A1*. The Site is bounded by Hollywood Road to the north, Arbuthnot Road to the east, Chancery Lane to the south and Old Bailey Street to the west.

The Site comprises three Declared Monuments designated under the *Antiquities and Monuments Ordinance* in 1995. They are:

- Central Police Station;
- Former Central Magistracy; and
- Victoria Prison Compound.

They are collectively named the Central Police Station (CPS). *Annex A2* shows the location of the Declared Monuments within CPS and the buildings within the CPS.

#### 2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in this reporting period is shown in *Table 2.1* and illustrated in *Annex A3*.

### Table 2.1Summary of Construction Activities undertaken in this Reporting Period

#### Construction Activities Undertaken

#### August 2017:

- Sitewide hard landscape construction;
- Timber elements repair and replacement at Blocks 1, 3, 6, 7, 9 and 14;
- Fitting out works at Blocks 1, 3, 6, 7, 9, 11, 14, 15, 17, Arbuthnot Wing and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 8, 9 and 14;
- External façade repair at Blocks 3, 9, 10, 12, 13 and 14;
- E&M fixing at Blocks 1, 3, 6, 7, 9, 12, 13, 14, 15, Arbuthnot Wing and Old Bailey Wing;
- Footbridge construction;
- Enhancement works at Blocks 3; and
- Guard house works construction.

#### September 2017:

- Sitewide hard landscape construction;
- Timber elements repair and replacement at Blocks 1, 3, 9, 10 and 14;
- Fitting out works at Blocks 3, 8, 9, 10, 11, 12, 13, 14, 17 and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 8, 9, 10, 12 and 14;
- External façade repair at Blocks 3, 9, 10, 12, 13, 14 and 17;
- E&M fixing at Blocks 1, 3, 6, 7, 9, 12, 13, 14, 15, Arbuthnot Wing and Old Bailey Wing;
- Footbridge construction; and
- Enhancement works at Blocks 3 and 10.

#### October 2017:

- Sitewide hard landscape construction;
- Timber elements repair and replacement at Blocks 3, 9, 10 and 14;
- Fitting out works at Blocks 3, 8, 9, 10, 11, 12, 13, 14, 17 and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 8, 9, 10, 12 and 14;
- External façade repair at Blocks 1, 3, 9, 10, 12, 13, 14 and 19;
- E&M fixing at Blocks 1, 3, 6, 7, 9, 12, 13, 14, 15, Arbuthnot Wing and Old Bailey Wing;
- Footbridge construction; and
- Enhancement works at Blocks 3, 8, 9, 10 and 14.

#### 2.4 CONSTRUCTION PROGRAMME

The most updated construction programme for the Project is presented in *Annex I*.

#### 2.5 PROJECT ORGANISATION AND MANAGEMENT STRUCTURE

The Project organization chart, hotline number and contact details are shown in *Annex B*.

#### 2.6 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the valid permits, licences, and/or notifications on environmental protection for this Project within the reporting period is presented in *Table 2.2*.

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Environmental Permit (EP)	EP-408/2011/C	Throughout the Contract	Permit granted on 29 April 2016
Notification of Construction Works as required under <i>Air</i> <i>Pollution Control</i> <i>(Construction Dust)</i> <i>Regulation</i>	Ref. No. 332920	Throughout the Contract	-
Registration of Chemical Waste Producer under <i>Waste</i> Disposal Ordinance	Chemical Waste Producer No.: 5213- 122-G2347-25	Throughout the Contract	-
Disposal of C&D material/waste	Billing Account Number: 7013338	Throughout the Contract	-
Effluent Discharge License under Water Pollution Control Ordinance	License No. WT00026824-2017	11 Jan 2017 - 31 Oct 2021	-
Notification of Commencement of Asbestos Abatement Work under <i>Air</i> <i>Pollution Control</i> <i>Ordinance</i>	-	Throughout the Contract	EPD's letter (EPD's ref.: (5) in EPAC/A/4/000/2 3 II) dated 2 December 2011 satisfied that the content of the asbestos abatement plan (Report No.: 0210/11/ED/0078. ) is in accordance with the APCO
Approval of Asbestos Abatement Work (Phase 2)	-	Earliest commencement date on 26 January 2012	EPD's letter (EPD's ref:() in EPAC/A/4/000/2 3) dated 18 January 2012.
Construction Noise Permit (CNP)	GW-RS0599-17	17 July 2017 at 1900 hours to 16 January 2018 at 2300 hours	-
	GW-RS0662-17	4 September 2017 at 2300 hours to 3 November 2017 at 0600 hours	-

## Table 2.2Summary of Environmental Licensing, Notification and Permit Status

#### 3 ENVIRONMENTAL MONITORING REQUIREMENTS

#### 3.1 NOISE MONITORING

#### 3.1.1 Monitoring Location

The construction noise monitoring locations are given in *Table 3.1* and shown in *Annex C*.

#### Table 3.1Construction Phase Noise Monitoring Locations

Monitoring Location	Proposed Construction Noise Monitoring Station			
	ID in EM&A Manual	ID	Type of Measurement	Remark
Rooftop of Ho Fook Building	N2	NM2	Façade	-
Rooftop of Chancery Mansion		NM6	Façade	Accesses to the original proposed monitoring location in the EM&A Manual, Chancery House (N5), were rejected; alternative location of Chancery Mansion (N6), were therefore proposed and approved by the Authorised Person (AP), the Independent Environmental Checker (IEC) and EPD.

The noise sensitive receivers are also shown in *Annex C*.

#### 3.1.2 Monitoring Parameters, Frequency and Programme

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. The monitoring programme for this reporting period is shown in *Annex D*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ) in decibels dB(A).  $L_{eq (30min)}$ were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays. Supplementary information for data auditing, two statistical sound levels  $L_{10}$  and  $L_{90}$ ; the levels exceeded for 10 and 90 percent of the time respectively, were also recorded during the monitoring for reference. The measured noise levels were logged in every 5 minutes throughout the impact monitoring period.

#### 3.1.3 Monitoring Equipment and Methodology

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures* of *Technical Memorandum on Noise from* 

*Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO)* (Cap 400).

The sound level meters and calibrator used for the noise measurement, as listed in *Table 3.2*, complies with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters are included in *Annex E*.

### Table 3.2Noise Monitoring Equipment

Monitoring Stations	Monitoring Equipment (Sound Level Meter and Calibrator)
NM2, NM6	<u>Calibrator</u> CEL-120 (S/N 3421612)
	Sound Level Meter
	CEL-633A (S/N 3521757)

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

Measurements were accepted as the calibration level from before and after the noise measurement agree to within 1.0 dB.

### 3.1.4 Event/Action Plan

### Table 3.3Action and Limit Levels for Construction Noise Monitoring

Noise Monitoring Location	Action Level	Limit Level, L <sub>eq(30mins), dB(A)</sub>	Remark
NM2, NM6	When one documented complaint is received from any one of the sensitive receivers	75 (note)	Applicable during 0700 – 1900 hours on normal weekdays.

a) Acceptable Noise Levels for Area Sensitivity Rating of A/B/C. Limit Level is reduced to 70dB(A) for schools and 65dB(A) during school examination periods.

b) If works are to be carried out during restricted hours, the conditions stipulated in the CNP issued by the NCA have to be followed.

The Event / Action Plan (EAP) for noise monitoring is presented in Annex F.

### 3.1.5 *Mitigation Measures*

The mitigation measures in accordance with the EP, EIA and EM&A Manual and their implementation status are presented in *Annex G*.

#### 3.2 CULTURAL HERITAGE

#### 3.2.1 Vibration Monitoring

In accordance with the EM&A Manual, vibration monitoring is required and the vibration control limits and vibration monitoring proposal are defined by a specialist for AMO's approval.

#### **Baseline Monitoring**

Baseline vibration monitoring was not conducted during the reporting period.

#### Vibration Monitoring for Demolition Works

As no demolition works were carried out, vibration monitoring for demolition works was not conducted during the reporting period.

#### Vibration Monitoring for Trial Piling and Pipe/Bored Piling Works

As no trial piling or pipe/bored piling works were carried out, vibration monitoring for trial piling and pipe/bored piling works was not conducted during the reporting period.

#### Vibration Monitoring for Other Construction Works

Vibration monitoring for specific construction works other than demolition works, trial piling works and pipe/bored piling works is also required in accordance with Building Department's requirement. The monitoring location is shown in *Annex L*. The number and location of monitoring location will depend on the location of the specific construction works. The vibration monitoring should be conducted for duration of 5 minutes on a daily basis (working day) at each vibration monitoring location.

#### Alert, Alarm and Action Levels

The Alert, Alarm and Action (AAA) Levels are to be implemented during the vibration monitoring and shown in *Table 3.4*.

#### Table 3.4Alert, Alarm and Action (AAA) Levels for Vibration Monitoring

Instrument Type	Item Monitored	Alert Level	Alarm Level	Action Level
Vibration Monitoring	Horizontal Movement	2.0 mm/s	2.5 mm/s	3.0 mm/s

The Event / Action Plan (EAP) for vibration monitoring is shown in Table 3.5.

#### Table 3.5Event and Action Plan for Vibration Monitoring

Events	Action
Exceedance of Alert Level	Notify Management Contractor
Exceedance of Alarm Level	Notify Authorised Person/ Resident Engineer

Events	Action
Exceedance of Action Level	Cease Works and submit mitigation

### 3.2.2 *Mitigation Measures*

Cultural heritage mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

### 3.3 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, inspections of affected trees were conducted by an experienced and appropriately trained arborist. All irregularities that deviate from the recommended tree protection measures or could impose deleterious impacts on the protected trees were reported. Besides, implementation of mitigation measures for landscape and visual resources recommended in the EIA Report were also monitored during the site inspection.

### 3.3.1 *Mitigation Measures*

Landscape and visual mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

### 3.4 Environmental Requirements in Contract Documents

The environmental requirements as specified in the contract documents were reviewed and were covered in the EIA's requirements.

# IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES

The Contractor has generally implemented the environmental mitigation measures (including those for archaeology) and requirements as stated in the EIA Report, EM&A Manual, EP and the contract documents. The implementation status during the reporting period is summarised in *Annex G*.

Status of required submissions under the EP during the reporting period is presented in *Table 4.1*.

Submission		Submission Date
EP Condition		
Conditions 3.4	• 69th Monthly EM&A Report	14 August 2017
	• 70 <sup>th</sup> Monthly EM&A Report	14 September 2017
	• 71 <sup>st</sup> Monthly EM&A Report	13 October 2017
EM&A Manual		
Section 10.4	• 23 <sup>rd</sup> Quarterly EM&A Report	24 October 2017

Table 4.1Status of Required Submissions

4

#### 5.1 NOISE

A total of 17 sets of 30-minute construction noise measurements were carried out at each monitoring station, NM2 and NM6, during normal weekdays of the reporting period. The monitoring results together with graphical presentations are presented in *Annex H*. The local impacts observed near the monitoring stations of NM2 and NM6 were summarised below:

- NM2: construction noise from activities in the Project Site and traffic noise from Old Bailey Street.
- NM6: construction noise from activities in the Project Site and traffic noise from Chancery Lane.

No exceedance of the Action or Limit Level of construction noise was recorded during the reporting period.

#### 5.2 LANDSCAPE AND VISUAL MONITORING

Three monthly tree inspections were conducted by the arborist during the reporting period on 4 August 2017, 5 September 2017 and 9 October 2017 and key findings and recommendations are summarised in *Table 5.1*.

#### Table 5.1Findings of Monthly Tree Inspections in the Reporting Period

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observation / Recommendations
4 August 2	2017		
Tree -5	Mangifera indica	Fair	• Signs of pests (Mealy Bugs) were observed on the tree.
			• Application of pesticides should be carried out as soon as possible.
Tree -6	Aleurites moluccana	Fair	• Signs of pest ( <i>Trialeurodes vaporariorum</i> ) apparently reduced due to pesticide application on 3 and 4 August 2017.
			• Leaves on the crown are rather sparse.
			• Keep monitoring on the growth of the tree.
Tree-7	Aleurites moluccana	Fair	• Signs of pest ( <i>Trialeurodes vaporariorum</i> ) apparently reduced due to pesticide application on 3 and 4 August 2017.
			• Leaves on the crown are rather sparse.
			• Keep monitoring on the growth of the tree.
Tree-8	Plumeria rubra	Good	• No further action required.
Tree-9	Araucaria cunninghamia	a Good	• No further action required.
Tree-11	Dracaena marginata	Fair	Remove construction debris away from

Tree No.	Botanical Name	Overall Health Condition	Arborist's Observation / Recommendations
			the planter.
			• Withered leaves were observed on the tree.
			• The Contractor should closely monitor the growth of the tree.
5 Septemb	per 2017		
Tree -5	Mangifera indica	Fair	• Signs of pests (Mealy Bugs) were observed on the tree.
			<ul> <li>Application of pesticides and pruning of decayed logs were conducted on 26 September 2017</li> </ul>
Tree -6	Aleurites moluccana	Fair	• Signs of pest ( <i>Trialeurodes vaporariorum</i> ) apparently reduced due to pesticide application on 3 and 4 August 2017.
			• Leaves on the crown are rather sparse.
			• Keep monitoring on the growth of the tree.
Tree-7	Aleurites moluccana	Fair	• Signs of pest ( <i>Trialeurodes vaporariorum</i> ) apparently reduced due to pesticide application on 3 and 4 August 2017.
			• Leaves on the crown are rather sparse.
			• Keep monitoring on the growth of the tree.
Tree-8	Plumeria rubra	Good	• No further action required.
Tree-9	Araucaria cunninghamia	a Good	• No further action required.
Tree-11	Dracaena marginata	Fair	<ul> <li>Construction debris observed in the last inspection has been removed from the planter.</li> </ul>
			<ul> <li>Withered leaves were observed on the tree.</li> </ul>
			• The Contractor should closely monitor the growth of the tree.
9 October	2017		
Tree -5	Mangifera indica	Fair	• No further action required.
Tree -6	Aleurites moluccana	Fair	• Leaves on the crown are rather sparse.
			• Four pits near the planter were created for ventilation purpose for the tree
			• Keep monitoring on the growth of the tree.
Tree-7	Aleurites moluccana	Fair	• Leaves on the crown are rather sparse.
			• Four pits near the planter were created for ventilation purpose for the tree
			• Keep monitoring on the growth of the tree.
Tree-8	Plumeria rubra	Good	• No further action required.
Tree-9	Araucaria cunninghamia	a Good	• No further action required.
Tree-11	Dracaena marginata	Fair	• Withered leaves were observed on the tree.
			• The Contractor should closely monitor the growth of the tree.

A Registered Consulting Arborist assessed Tree 6 and Tree 7 on 12 August 2017 and commented that the pests on the trees appeared to be under control

after the pesticide application on 3 and 4 August 2017. He also advised that further application of pesticides on Tree 6 and Tree 7 would not be necessary at the moment but should keep close monitoring of the effectiveness of the pesticide and the health of the trees.

Follow-up actions needed to be implemented were recommended to the Contractor and the status of the follow-up actions was reviewed during the subsequent monthly site inspections. Recommendations have generally been implemented by the Contractor during the reporting period.

## 5.3 CULTURAL HERITAGE

### 5.3.1 Vibration Monitoring

No vibration monitoring was carried out for demolition works, trial piling or pile/bored piling works as the aforementioned works were not conducted during the reporting period.

### Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

### August 2017:

• 26 vibration monitoring measurements for the structural addition and alteration works at Block 11.

### September 2017:

• 26 vibration monitoring measurements for the structural addition and alteration works at Block 11.

### October 2017:

• 23 vibration monitoring measurements for the structural addition and alteration works at Block 11.

The monitoring results are presented in Annex L.

All monitoring results were below the Alert/Alarm/ Action Levels during the reporting period.

### 5.3.2 Heritage Site Audit

Heritage site audits were conducted on every working weekday by the Heritage Checker during the reporting period. Key site audit findings and recommendations are summarised below. The Contractor was urged to follow-up the necessary rectification based on the inspection findings.

16 August 2017

• It was observed that the waterproofing at roof of Block 13 was damaged. The Contractor was reminded to repair the waterproofing to protect the building.

### 22 August 2017

• It was observed that the wall on second floor of Block 13 was saturated below the former canopy location, indicating water ingress from the canopy. The Contractor was reminded to repair the canopy to protect the building.

### 29 August 2017

- It was observed that the wall at the southeast corner of Block 4 was saturated with water causing damage on brickwork. The Contractor was reminded to follow up and provide proper protection.
- It was observed that the wall and floor at Block 17 south and Block 3 new bridge was not properly protected. The Contractor was reminded to provide sufficient protection.

## 30 August 2017

• It was observed that the glazing at ground floor of Block 3 was not properly protected. The Contractor was reminded to follow up and provide proper protection to the glazing.

## 7 September 2017

• It was observed that the waterproofing at roof of Blocks 11 and 13 was damaged. The Contractor was reminded to repair the waterproofing to protect the building.

## 28 September 2017

• Improvement of tidiness at Magistracy Terrace is required. The Contractor was reminded to follow up.

## 29 September 2017

- It was observed that the waterproofing material used for roof of Block 14 was of substandard quality. The Contractor was reminded to rectify the defective waterproofing to protect the building.
- A pond of stagnant water was observed on ground floor north terrace of Block 1, which may cause potential damage to floor tiles. The Contractor was reminded to remove the stagnant water.
- Saturation of wall at Block 9 was observed due to inadequate temporary rainwater pipe. The Contractor was reminded to complete the

rainwater pipe installation or extend the temporary rainwater pipe to protect the adjacent wall.

• It was observed that the wall on second floor of Block 13 was saturated below the former canopy location, indicating water ingress from the canopy. The Contractor was reminded to repair the canopy to protect the building.

### 9 October 2017

• It was observed that no protection was provided to the finished tiled floor at lower ground level of Block 1. The Contractor was reminded to provide adequate protection to the tiled floor.

### 12 October 2017

• It was observed that no protection was provided to the graffiti on first floor of Block 14. The Contractor was reminded to provide adequate protection.

### 17 October 2017

• Water ponding and re-bar rusting due to incomplete repair were observed at ladder store canopy at Block 13. The Contractor was reminded to follow up.

### 19 October 2017

• It was observed that window repairs at east elevation of Block 15 were not completed prior to removal of scaffold and the window was in defective condition. The Contractor was reminded to follow up.

## 20 October 2017

- It was observed that a worker was using electric breaker to remove paint from the wall at Block 14 and the worker was stopped immediately. The Contractor was reminded to follow up.
- It was observed that protection was not provided during concreting at Block 3. Protection was immediately provided after reminder.

## 31 October 2017

• Three timber doors were observed split at Block 7, indicating that the timber drying out process was not handled properly. The Contractor was reminded to carry out rectification works to the timber doors.

No non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period. The summary of condition of the character defining elements, historic buildings and structures is contained in *Annex M*.

#### 5.4 WASTE MANAGEMENT

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. Non-inert C&D materials were made up of wastes such as general refuse and mixed construction waste. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in *Table 5.2.* The summary of Waste Flow Table prepared by the Contractor is shown in Annex J. No metal, paper/cardboard packaging or plastic waste was recycled during the reporting period. No chemical waste was collected by licenced chemical waste collector during the reporting period.

Month / Year	Quantity						
	C&D	C&D Chemical Materials Waste		Recycled materials			
	Materials			ste			
	(inert)	(non-inert)	Liquid	Solid	Paper/	Plastics	Metals
	(tonnes) <sup>(a)</sup>	(tonnes) (b)	(L)	(kg)	cardboard (kg)	(kg)	(kg)
August 2017	79.39	58.03	0	0	0	0	0
September 2017	199.78	62.43	0	0	0	0	0
October 2017	103.07	50.09	0	0	0	0	0
Total	382.24	170.55	0	0	0	0	0

#### Table 5.2 Quantities of Waste Generated from the Project

Notes:

(a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. The inert C&D materials were sent to Chai Wan Public Fill Barging Point and Tseung Kwan O Area 137 Fill Bank.

(b) Non-inert C&D materials include general refuse and mixed construction waste. The noninert C&D materials were disposed of at SENT Landfill and Tseung Kwan O Area 137 Sorting Facility

#### 5.5 **EFFECTIVENESS OF MITIGATION MEASURES AND MONITORING**

The mitigation measures recommended in the EIA report and required by the EP are considered effective in minimising environmental impacts.

The EM&A for the Project was conducted as scheduled during the reporting period. No non-compliance events were observed during site inspections and no exceedances of action or limit level were recorded during the reporting period. The EM&A programme is considered effective.

Three monthly environmental site inspections were conducted on 24 August 2017, 18 September 2017 and 26 October 2017 during the reporting period. There was no non-compliance recorded during the site inspections. Key observations and recommendations are summarised below. The recommendations were implemented and the observations were rectified by the Contractor in the subsequent monthly site inspection.

24 August 2017

• Nil

6

An ad-hoc joint tree inspection for Tree 6 and Tree 7 was carried out by the representatives of the arborist, Contractor, IEC, ET, HKJC, EPD and relevant parties on 8 August 2017.

18 September 2017

• Nil

26 October 2017

• Nil

This page is deliberately left blank

#### 7 ENVIRONMENTAL NON-CONFORMANCE

### 7.1.1 Summary of Monitoring Exceedance

No exceedance of the Action or Limit Level of construction noise or Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

### 7.1.2 Summary of Enquiry

An enquiry was recorded regarding a published article on 31 July 2017 and a follow-up article on 5 August 2017 by Ming Pao. An investigation has been carried out to address the Ming Pao reports during the reporting period. The 31 July 2017 article indicated that pests were found on Tree 6 and 7 and the current amount of leaves on Tree 6 and Tree 7 have seemingly reduced in comparison with the photo of the trees which was said to be taken in December 2015, suggesting that the health of Tree 6 and Tree 7 may have deteriorated. The report enquired if the construction work has been carried out in compliance with the requirements in the Environmental Permit and potential measures to rectify the condition of Tree 6 and Tree 7. The 5 August 2017 article reported that the contractor has applied pesticides to the trees but queried if the contractor did not rectify the problem in a timely manner. An ad-hoc joint tree inspection for Tree 6 and Tree 7 was carried out by the representatives of the arborist, Contractor, IEC, ET, HKJC, EPD and relevant parties on 8 August 2017. An investigation has been carried out to address the Ming Pao reports and the investigation report is provided in Annex K. The recommended follow-up actions are being implemented.

### 7.1.3 Summary of Non-Compliance

No environmental non-compliance event was recorded during the reporting period. No non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period.

#### 7.1.4 Summary of Environmental Complaint

No complaint was received during the reporting period. The cumulative number of complaints is presented in *Annex K*.

### 7.1.5 Summary of Environmental Summons and Successful Prosecution

No summons was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex K*.

This page is deliberately left blank

#### 8.1 NOISE

A comparison was made between the monitoring results in this reporting period and the Noise Standard for general construction works during 0700 – 1900 hrs on normal weekdays (*Table 8.1*).

Table 8.1 Co

Comparison of Construction Noise Standard and Noise Monitoring Results

Reporting Month	Monitoring Stations	Corresponding NSR in EIA	Noise Limit Level	Predicted Construction Noise Level (With Mitigation) in EIA		
			L <sub>eq, 30 min</sub> dB(A)	L <sub>eq, 30 min</sub> dB(A)	L <sub>eq, 30 min</sub> dB(A)	
August	NM2	N2	75	67 - 72	65.5 - 69.1	
2017	NM6	N6	75	73 - 75	62.1 - 66.3	
September	NM2	N2	75	67 - 72	67.0 - 69.8	
2017	NM6	N6	75	73 - 75	63.6 - 65.4	
October 2017	NM2	N2	75	67 - 72	65.9 - 69.1	
	NM6	N6	75	73 - 75	62.6 - 65.3	

The monitoring results recorded since the commencement of the construction works have been below the Limit Level and comparable to the predicted construction noise level in the approved EIA. Recommended mitigation measures in *Section 5.9.1* of EIA will continue to be implemented throughout the construction stage.

#### 8.2 WASTE MANAGEMENT

The estimated amount of waste generated in the approved EIA and the accumulated quantities of waste generated up to this reporting period are presented in *Table 8.2*. The accumulated amount of inert and non-inert C&D materials is higher than the estimated amount in EIA. The major chemical waste generated on site was primarily asbestos which was not estimated in the approved EIA and hence no data is available for comparison. Recommended mitigation measures in *Section 8.5.1* of the EIA will continue to be implemented throughout the construction stage.

# Table 8.2Quantity of Actual Amount of C&D Materials, General Wastes and Chemical<br/>Wastes Generated and EIA Estimation

Type of Material	Estimated Amount of Waste in EIA	Accumulated Actual Amount of Waste Recorded <sup>(a) (b)</sup>		
Amount of C&D Materials (Inert) Arising	16,440 m <sup>3</sup>	37,898.25 m <sup>3</sup>		
Amount of C&D Materials (Non-inert) Arising	890 m <sup>3</sup>	15,634.13 m <sup>3</sup>		
General Refuse	130 kg per day	_ (c)		
Chemical Waste	Less than 100L per month	<ul> <li>57 L (liquid)</li> <li>395 kg (solid)</li> <li>7,000 kg of asbestos generated</li> </ul>		

#### Notes:

(a) The accumulated actual amount of C&D Materials and chemical waste were recorded since the commencement of construction works.

(b) The volume of waste materials are provided by the Contractor based on the updated waste record in October 2017.

(c) The amount of general refuse generated was not recorded.

#### 8.3 SUMMARY OF REVIEW

The EIA predictions and the monitoring results since the commencement of construction works have been reviewed. The EIA concluded that the Project would not cause adverse impacts to the environment and the monitoring results have also indicated the same so far. Mitigation measures (including those for archaeology) recommended in the EP, EIA and EM&A Manual were implemented by the Contractor as far as practicable and were considered effective. The recommended mitigation measures will continue to be implemented throughout the construction phase of the Project.

The effectiveness of the monitoring programme has been exhibited therefore change to the programme is not considered to be necessary.

#### CONCLUSIONS

9

This 24<sup>th</sup> Quarterly EM&A Report presents the EM&A works undertaken during the reporting period from 1 August 2017 to 31 October 2017 in accordance with the EM&A Manual.

No exceedance of the Action or Limit Level of construction noise was recorded at designated monitoring stations during the reporting period.

Tree inspections were conducted in this reporting period. Most of the necessary landscape and visual mitigation measures recommended in the EIA Report were implemented by the Contractor.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

An enquiry was recorded regarding a published article on 31 July 2017 and a follow-up article on 5 August 2017 by Ming Pao. An investigation has been carried out to address the Ming Pao reports during the reporting period. The recommended follow-up actions are being implemented.


No environmental non-compliance event was recorded during the reporting period. No non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period.


No complaint was received during the reporting period.

No summons/prosecution was received during the reporting period.


The monitoring programme was considered effective in reflecting the environmental conditions at the designated representative sensitive receivers. The monitoring results also indicate that the Project have not caused adverse impacts on the environment with implementation of appropriate mitigation measures. Change to the monitoring programme is not considered to be necessary. The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures in the coming periods. Annex A

Locations of Works Areas and the Surroundings

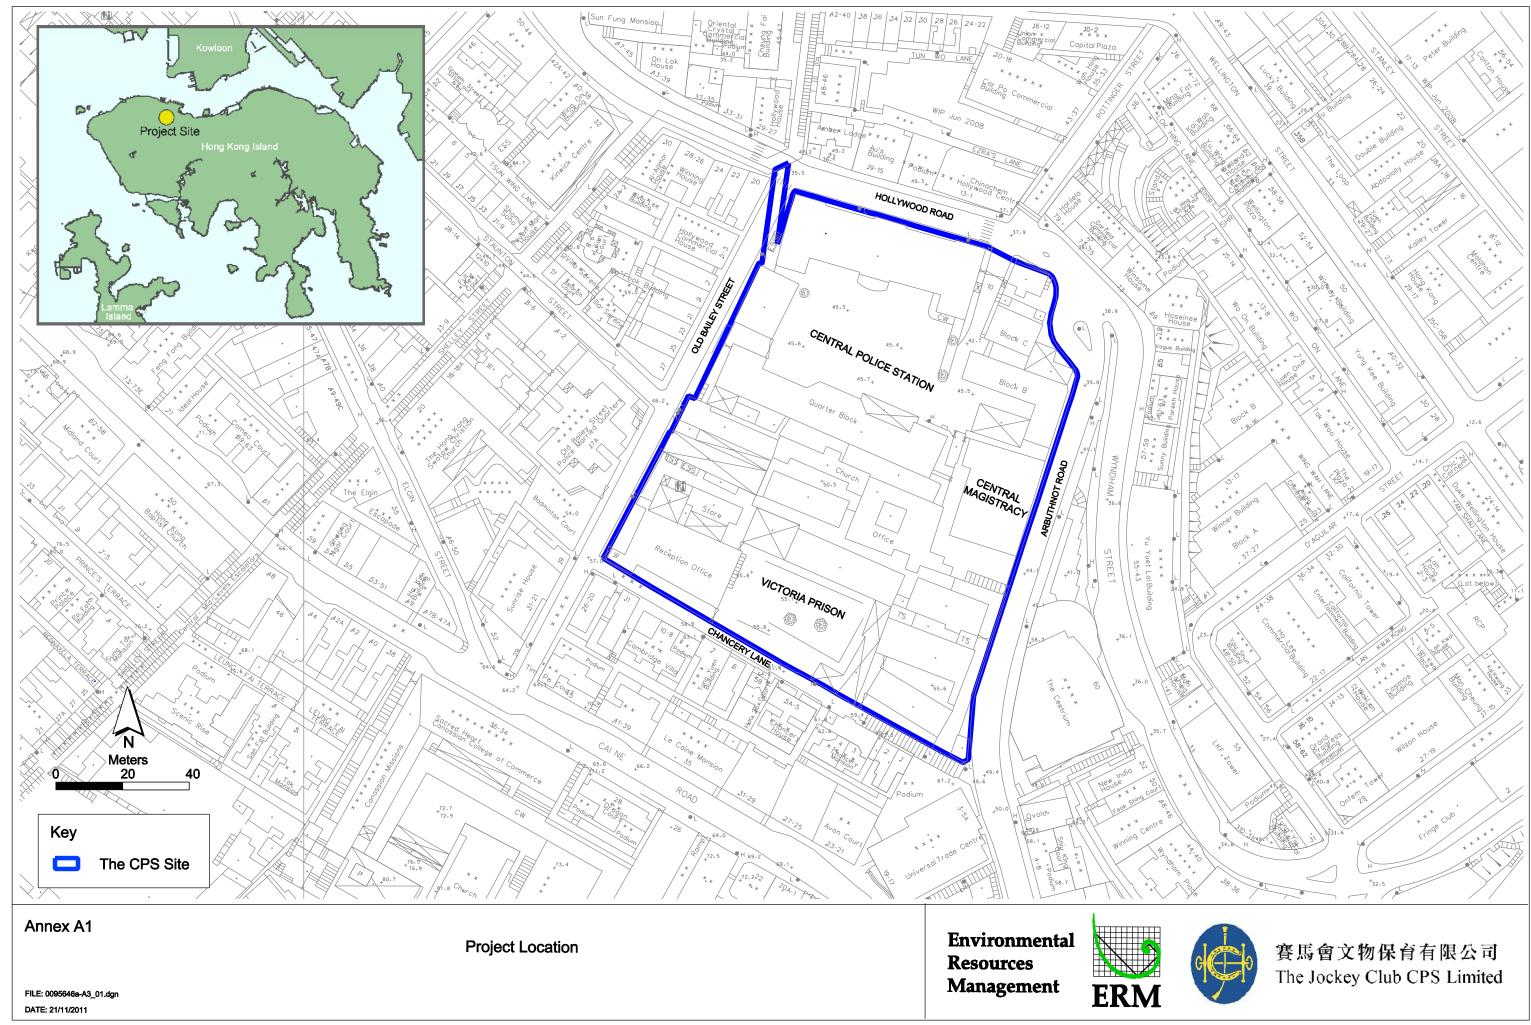

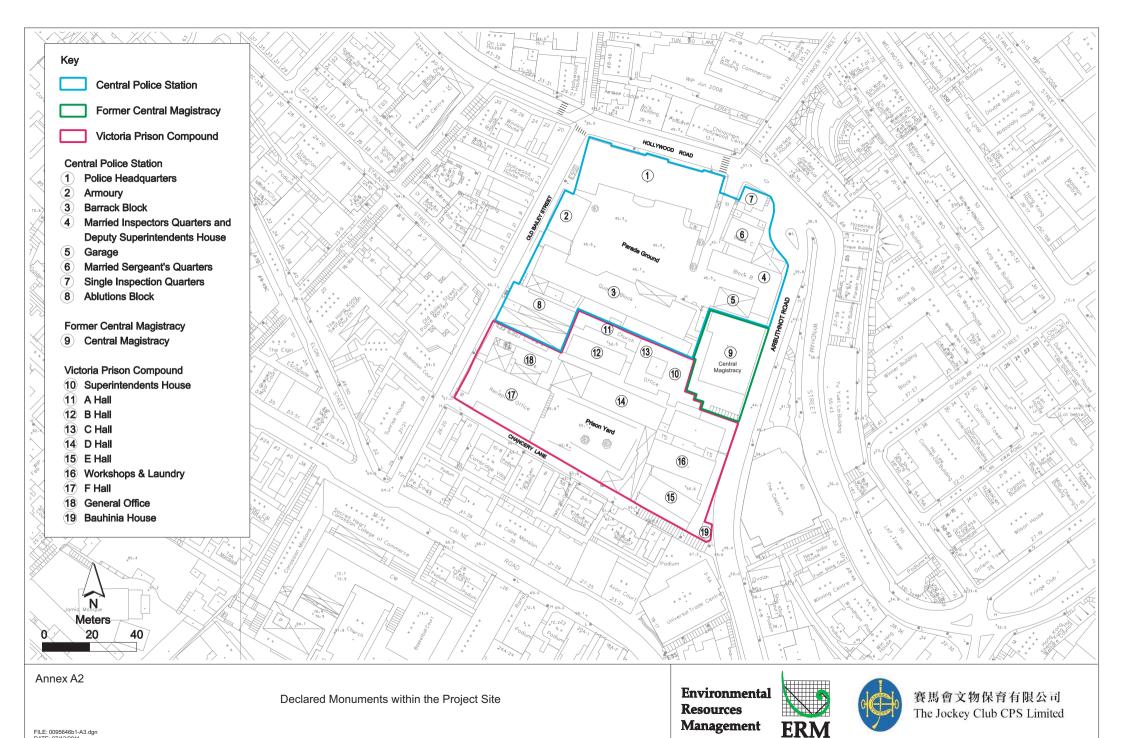


FILE: 0095646b1-A3.dgn DATE: 07/12/2011

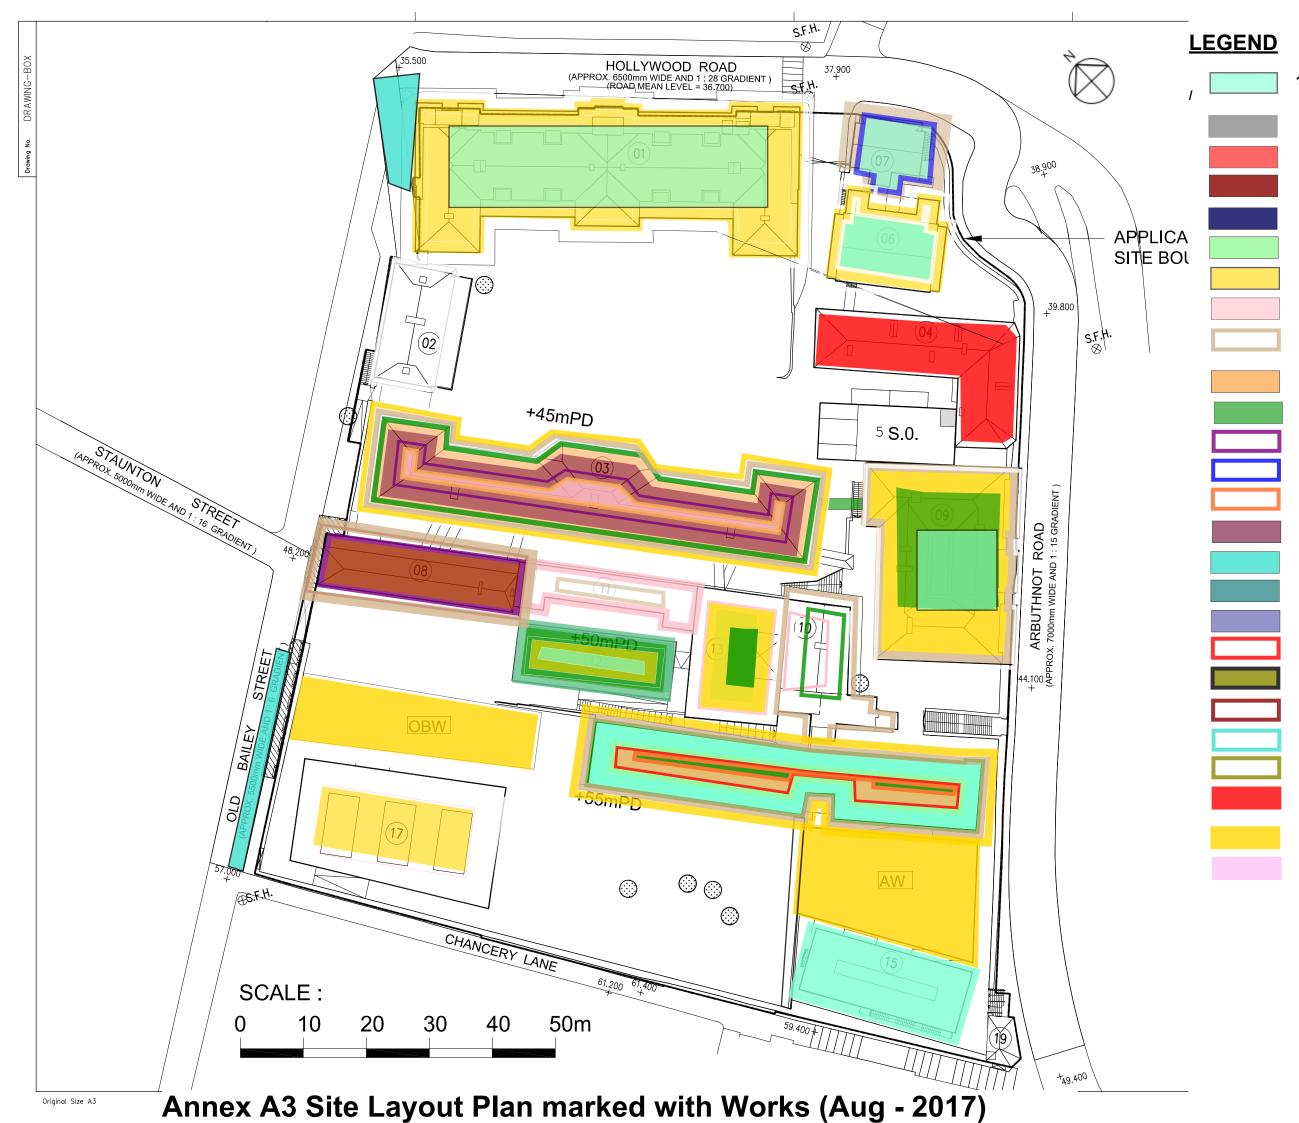

- 1. E&M Installation / Opening / Conduit Transformer delivery and installation
- 2. Excavation
- 3. Internal Building Works
- 4. Permanent Steel Works Erection
- 5. Upgrading
- 6. Roof Replacement Works / New Roof / Repair
- 7. Basement Construction
- 8. Structure A&A Works

9. Repair Works to Timber Window, Door, Structure, Floor and Metal Elements


- **10. Demolition Works**
- 11. Facade Works / Link Bridage Repair
- **12. New Structure Construction**
- 13. Balcony Repair
- 14. Paint Stripping and Plastering Works
- 15. Core Wall Construction
- 16. Utilities Diversion and Carriageway
- 17. PBR
- 18. Removal of Needle Beams
- 19. U/G Drainage
- 20. Service trench construction
- 21. Demolition of concrete block
- 22. New Balcony Construction
- 23. Construction of terminal Manhole
- 24. Emergency Works for collasped building and BD inspection
- 25. Fitting Out Works / E&M Fixing
- 26. Enhancement Works

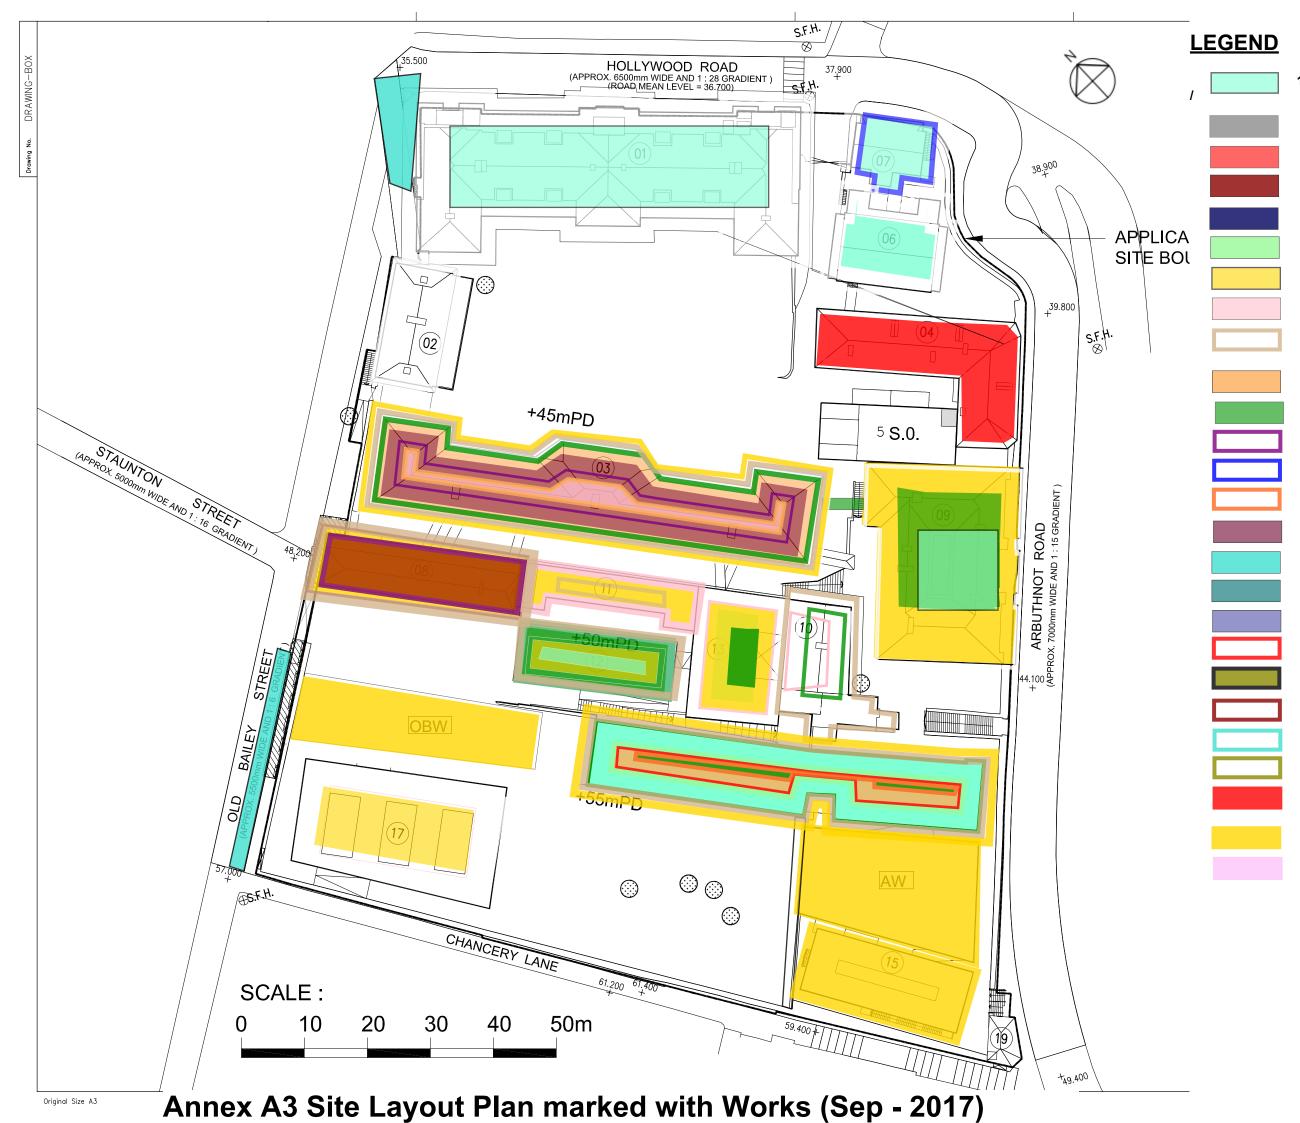

- 1. E&M Installation / Opening / Conduit Transformer delivery and installation
- 2. Excavation
- 3. Internal Building Works
- 4. Permanent Steel Works Erection
- 5. Upgrading
- 6. Roof Replacement Works / New Roof / Repair
- 7. Basement Construction
- 8. Structure A&A Works

9. Repair Works to Timber Window, Door, Structure, Floor and Metal Elements

- **10. Demolition Works**
- 11. Facade Works / Link Bridage Repair
- **12. New Structure Construction**
- 13. Balcony Repair
- 14. Paint Stripping and Plastering Works
- 15. Core Wall Construction
- 16. Utilities Diversion and Carriageway
- 17. PBR
- 18. Removal of Needle Beams
- 19. U/G Drainage
- **20. Service trench construction**
- 21. Demolition of concrete block
- 22. New Balcony Construction
- 23. Construction of terminal Manhole
- 24. Emergency Works for collasped building and BD inspection
- 25. Fitting Out Works / E&M Fixing
- 26. Enhancement Works

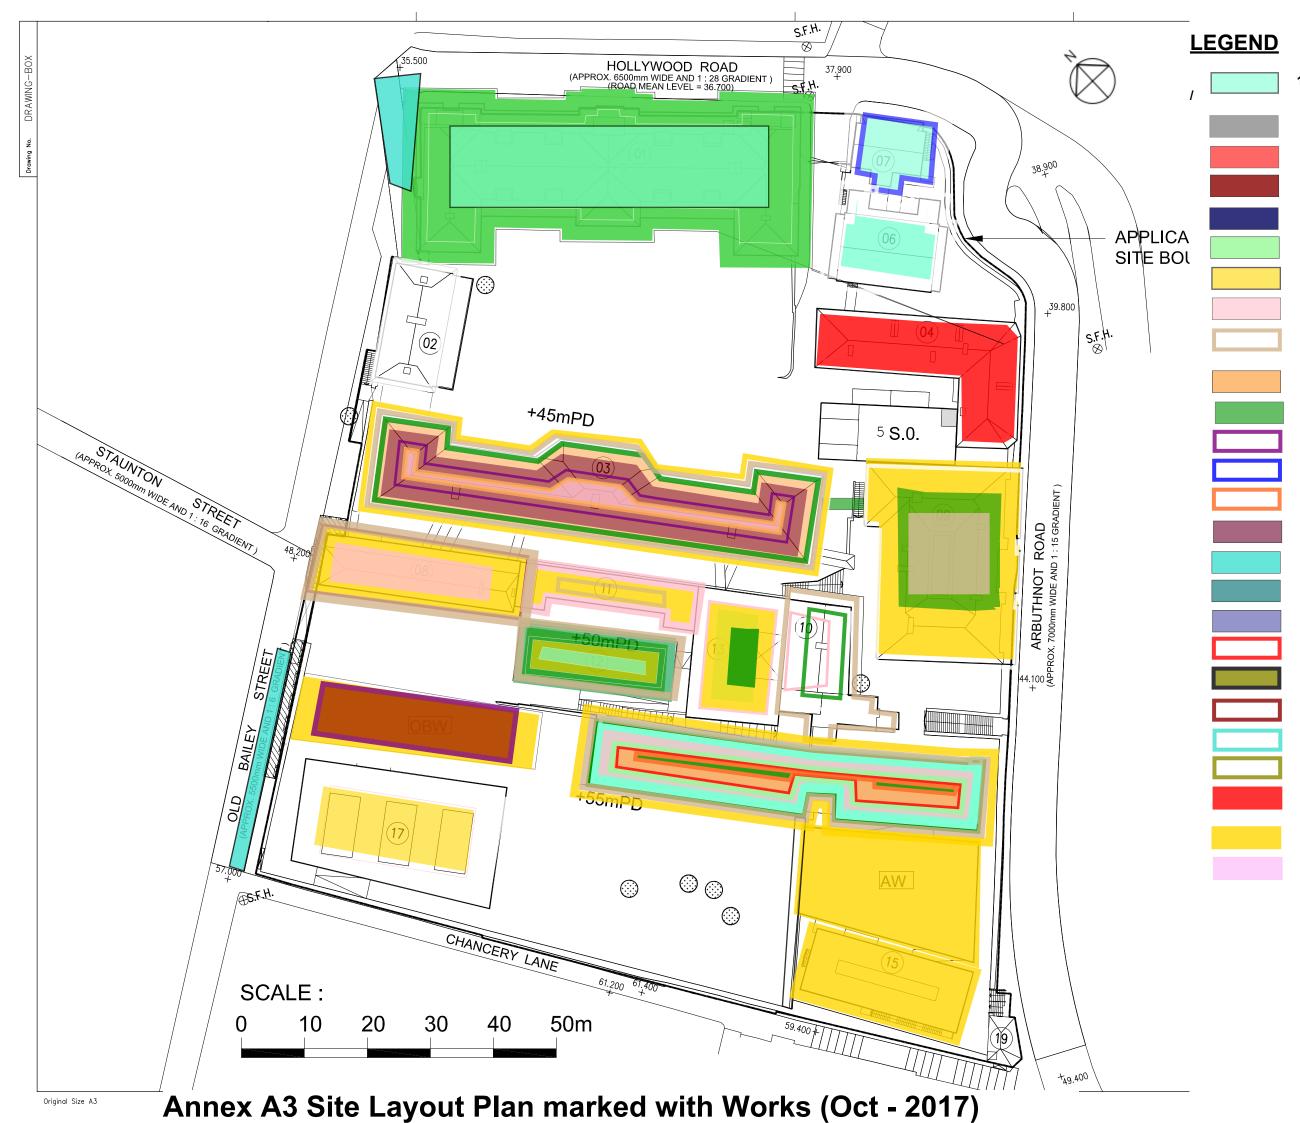


- 1. E&M Installation / Opening / Conduit Transformer delivery and installation
- 2. Excavation
- 3. Internal Building Works
- 4. Permanent Steel Works Erection
- 5. Upgrading
- 6. Roof Replacement Works / New Roof / Repair
- 7. Basement Construction
- 8. Structure A&A Works

9. Repair Works to Timber Window, Door, Structure, Floor and Metal Elements

- **10. Demolition Works**
- 11. Facade Works / Link Bridage Repair
- **12. New Structure Construction**
- 13. Balcony Repair
- 14. Paint Stripping and Plastering Works
- 15. Core Wall Construction
- 16. Utilities Diversion and Carriageway
- 17. PBR
- 18. Removal of Needle Beams
- 19. U/G Drainage
- **20. Service trench construction**
- 21. Demolition of concrete block
- 22. New Balcony Construction
- 23. Construction of terminal Manhole
- 24. Emergency Works for collasped building and BD inspection
- 25. Fitting Out Works / E&M Fixing
- 26. Enhancement Works


Annex B

Project Organization Chart and Contact Detail

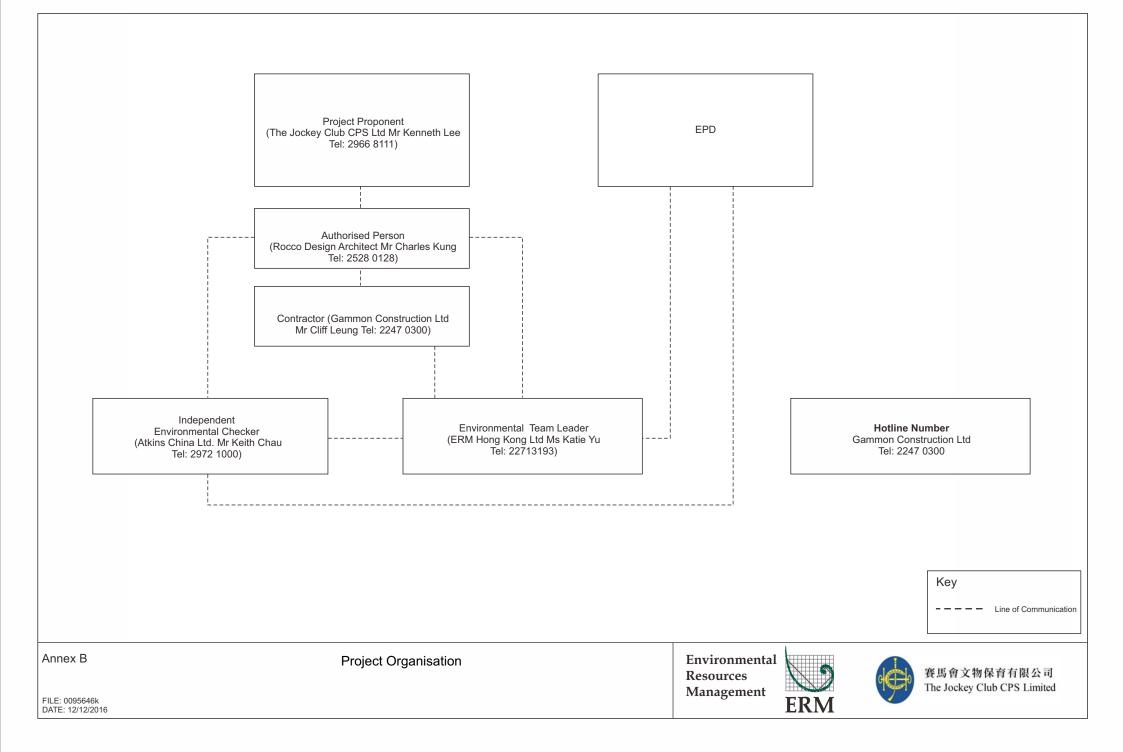

Annex C

Locations of Noise Monitoring Stations and Noise Sensitive Receivers

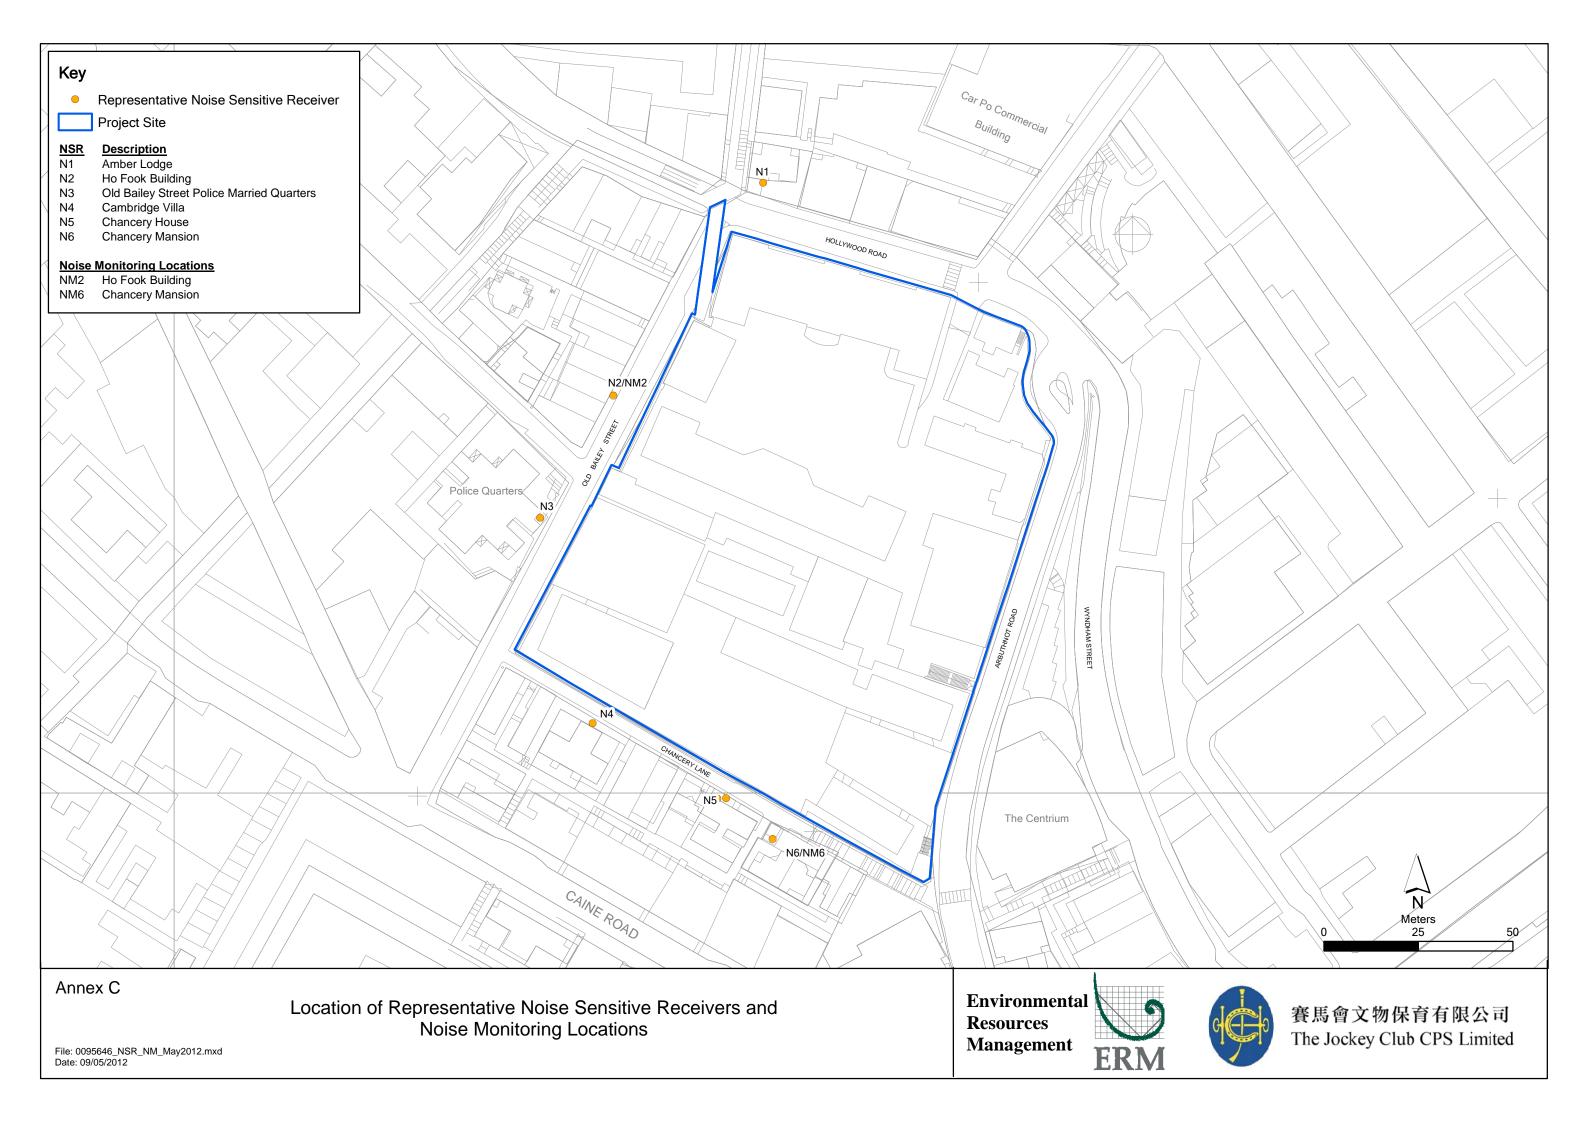

Annex D

Monitoring Schedule of the Reporting Period and Next Month

### Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - August 2017

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		01-Aug	02-Aug	03-Aug	04-Aug	05-Aug
				Noise Monitoring at NM2 & NM6		
06-Aug	07-Aug	08-Aug	09-Aug	10-Aug	11-Aug	12-Aug
			Noise Monitoring at NM2 & NM6			
13-Aug	14-Aug	15-Aug	16-Aug	17-Aug	18-Aug	19-Aug
		Noise Monitoring at NM2 & NM6				
20-Aug	21-Aug	22-Aug	23-Aug	24-Aug	25-Aug	26-Aug
	Noise Monitoring at NM2 & NM6				Noise Monitoring at NM2 & NM6	
27-Aug	28-Aug	29-Aug	30-Aug	31-Aug		
				Noise Monitoring at NM2 & NM6		

### Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - September 2017

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					01-Sep	02-Sep
03-Sep	04-Sep	05-Sep	06-Sep	07-Sep	08-Sep	09-Sep
			Noise Monitoring			
			at NM2 & NM6			
10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep	16-Sep
		12 000	10 000		10 000	10 000
		Noise Monitoring				
		at NM2 & NM6				
17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep	23-Sep
	Noise Monitoring				Noise Monitoring	
	at NM2 & NM6				at NM2 & NM6	
24-Sep	25-Sep	26-Sep	27-Sep	28-Sep	29-Sep	30-Sep
				Noise Monitoring at NM2 & NM6		
				$\alpha$ iniviz $\alpha$ inivio		

#### Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - October 2017

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
01-Oct	02-Oct	03-Oct	04-Oct	05-Oct	06-Oct	07-Oct
		Noise Monitoring at NM2 & NM6				
08-Oct	09-Oct	10-Oct	11-Oct	12-Oct	13-Oct	14-Oct
	Noise Monitoring at NM2 & NM6				Noise Monitoring at NM2 & NM6	
15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct	21-Oct
				Noise Monitoring at NM2 & NM6		
22-Oct	23-Oct	24-Oct	25-Oct	26-Oct	27-Oct	28-Oct
			Noise Monitoring at NM2 & NM6			
29-Oct	30-Oct	31-Oct				
		Noise Monitoring at NM2 & NM6				

Annex E

Calibration Reports for Calibrators and Sound Level Meters



0

Sun Creation Engineering Limited


Calibration and Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No.: C166691 證書編號

Manufacturer / 製 Model No. / 型號 Serial No. / 編號 Supplied By / 委討	ž : :	(Job No. / 序引編號: IC16- Acoustic Calibrator Casella CEL-120/1 3421612 Envirotech Services Co. Room 113, 1/F, My Loft, 9 He New Territories, Hong Kong	s.	201
<b>TEST CONDIT</b> Temperature / 溫 Line Voltage / 電	度: (23	式條件 3 ± 2)°C	Relative Humidity / 相對濕度 : (55 =	± 20)%
TEST SPECIFIC		/測試規範		
DATE OF TEST	Г/測試日期	月 : 30 November 2016		
The results do no	to the parti of exceed ma	cular unit-under-test only. nufacturer's specification.	-	
The results are de	etailed in the	e subsequent page(s).		
The test equipme - The Governme	ent used for ent of The H ologies / Ke varz Laborat	calibration are traceable to Nati ong Kong Special Administrati ysight Technologies ory, Germany	onal Standards via : ve Region Standard & Calibration Laboratory	
The test equipme - The Governme - Agilent Techno - Rohde & Schw	ent used for ent of The H ologies / Ke varz Laborat	calibration are traceable to Nati ong Kong Special Administrati ysight Technologies ory, Germany		

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration and Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No. : C166691 證書編號

1

3

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- 2. The results presented are the mean of 3 measurements at each calibration point.
- 3. Test equipment :

Equipment ID	Description	Certificate No.
CL130	Universal Counter	C163709
CL281	Multifunction Acoustic Calibrator	PA160023
TST150A	Measuring Amplifier	C161175

- 4. Test procedure : MA100N.
- 5. Results :
- 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.1	± 0.25	± 0.2
114 dB, 1 kHz	114.1		

### 5.2 Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's	Uncertainty of Measured Value
(kHz)	(kHz)	Spec.	(Hz)
1	1.000 0	$1 \text{ kHz} \pm 5 \text{ Hz}$	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration and Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No. : C166692 證書編號

Description / 儀器 Manufacturer / 製製 Model No. / 型號 Serial No. / 編號 Supplied By / 委討	名稱 : 造商 : :	(Job No. / 序引編號: IC16-2717 Sound Level Meter Casella CEL-633A 3521757 Envirotech Services Co. Room 113, 1/F, My Loft, 9 Hoi W New Territories, Hong Kong		)16
TEST CONDITIO Temperature / 溫月 Line Voltage / 電風	芰: (2	式條件 3 ± 2)°C	Relative Humidity / 相對濕度 : (55 ± 20	)%
TEST SPECIFIC Calibration check	ATIONS	/ 測試規範		
DATE OF TEST	/ 測試日期	期 : 30 November 2016		ų
TEST RESULTS			-	
The results do not	exceed ma	cular unit-under-test only. anufacturer's specification. e subsequent page(s).		
- The Governmen	t of The H ogies / Ke rz Laborat	ysight Technologies tory, Germany	Standards via : gion Standard & Calibration Laboratory	
Tested By 測試	: _	H T Wong Technical Officer		
		2		



Sun Creation Engineering Limited

Calibration and Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No. : C166692 證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration using the Casella Acoustic Calibrator CEL-120/1, S/N : 3421612 was performed before the test.
- 3. The results presented are the mean of 3 measurement at each calibration point.
- 4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C160077
CL281	Multifunction Acoustic Calibrator	PA160023

- 5. Test procedure : MA101N.
- 6. Results :
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

UUT Setting		Applied Value		UUT	IEC 61672 Class 1
Time	Frequency	Level	Freq.	Reading	Spec.
Weighting	Weighting	(dB)	(kHz)	(dB)	- (dB)
L <sub>F</sub>	A	114.00	1	113.7	± 1.1

#### 6.1.2 Linearity

UUT	Setting	Applied Value		Setting Applied Value		UUT
Time Weighting	Frequency Weighting	Level (dB)	Freq. (kHz)	Reading (dB)		
L <sub>F</sub>	A	114.00	1	113.7 (Ref.)		
		104.00		103.7		
1		94.00		93.5		

IEC 61672 Class 1 Spec. :  $\pm$  0.6 dB per 10 dB step and  $\pm$  1.1 dB for overall different.

#### 6.2 Time Weighting

UUT	UUT Setting		d Value	UUT	IEC 61672 Class 1
Time	Frequency	Level	Freq.	Reading	Spec.
Weighting	Weighting A	(dB) 114.00	(kHz)	(dB) 113.7	(dB) Ref.
L <sub>F</sub> L <sub>s</sub>	A	117.00	•	113.7	± 0.3

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 – 校正及檢測實驗所 c/o 香港新界屯門興安里一號青山灣機樓四樓 Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab/@suncreation.com Website'網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

# Certificate of Calibration 校正證書

Certificate No. : C166692 證書編號

### 6.3 Frequency Weighting

#### 6.3.1 A-Weighting

UUT	Setting	App	lied Value	UUT	SIEC 61672 Class 1
Time Weighting	Frequency Weighting	Level (dB)	Freq.	Reading (dB)	Spec. (dB)
L <sub>F</sub>	A	94.00	63 Hz	87.4	$-26.2 \pm 1.5$
			125 Hz	97.5	$-16.1 \pm 1.5$
			250 Hz	105.0	$-8.6 \pm 1.4$
			500 Hz	110.4	$-3.2 \pm 1.4$
			1 kHz	113.7	Ref.
			2 kHz	114.9	$+1.2 \pm 1.6$
			4 kHz	114.6	$+1.0 \pm 1.6$
			8 kHz	112.2	-1.1(+2.1;-3.1)
			12.5 kHz	108.1	-4.3(+3.0;-6.0)

### 6.3.2 C-Weighting

UUT	Setting	App	lied Value	UUT	IEC 61672 Class 1
Time	Frequency	Level	Freq.	Reading	Spec.
Weighting	Weighting	(dB)		(dB)	(dB)
L <sub>F</sub>	С	94.00	63 Hz	112.8	$-0.8 \pm 1.5$
			125 Hz	113.5	$-0.2 \pm 1.0$
			250 Hz	113.7	$0.0 \pm 1.0$
			500 Hz	113.7	0.0 ± 1.0
			1 kHz	113.7	Ref.
			2 kHz	113.5	$-0.2 \pm 1.0$
			4 kHz	112.8	$-0.8 \pm 1.0$
			8 kHz	110.4	-3.0 (+1.5 ; -3.0)
			12.5 kHz	106.2	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。



Sun Creation Engineering Limited

Calibration and Testing Laboratory

### Certificate of Calibration 校正證書

Certificate No. : C166692 證書編號

Remarks : - UUT Microphone Model No. : CEL-251 & S/N : 1950

- Mfr's Spec. : IEC 61672 Class 1 - Uncertainties of Applied Value : 114 dB : 63 Hz - 125 Hz  $: \pm 0.45 \, dB$ 250 Hz - 500 Hz : ± 0.40 dB 1 kHz : ± 0.30 dB 2 kHz - 4 kHz : ± 0.45 dB 8 kHz  $: \pm 0.55 \, dB$ 12.5 kHz  $: \pm 0.80 \text{ dB}$ 104 dB : 1 kHz  $: \pm 0.10 \text{ dB}$  (Ref. 114 dB) 94 dB : 1 kHz  $:\pm 0.10 \text{ dB}$  (Ref. 114 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

Annex F

# Event / Action Plans for Noise

### Annex F Event and Action Plan for Noise

Event	Action							
	En	vironmental Team (ET)		dependent Environmental necker (IEC)	A	uthorised Person (AP)	C	ontractor
Action Level	1. 2. 3. 4. 5.	Notify IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, AP and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness.	<ol> <li>1.</li> <li>2.</li> <li>3.</li> </ol>	Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the AP accordingly; Supervise the implementation of remedial measures.	<ol> <li>1.</li> <li>2.</li> <li>3.</li> <li>4.</li> </ol>	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to proposed remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented.	1. 2.	Submit noise mitigation proposals to IEC; Implement noise mitigation proposals.
Limit Level	<ol> <li>1.</li> <li>2.</li> <li>3.</li> <li>4.</li> <li>5.</li> <li>6.</li> <li>7.</li> <li>8.</li> </ol>	Identify source; Inform IEC and AP; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, AP and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and AP informed of the results; If exceedance stops, cease additional monitoring.		Discuss amongst AP, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the AP accordingly; Supervise the implementation of remedial measures.	<ol> <li>1.</li> <li>2.</li> <li>3.</li> <li>4.</li> <li>5.</li> </ol>	Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	<ol> <li>1.</li> <li>2.</li> <li>3.</li> <li>4.</li> <li>5.</li> </ol>	Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the AP until the exceedance is abated.

Annex G

Summary of Implementation Status

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultur	al Heritag	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	V
S3.9.2	S3.3.1	<u>Vibration Monitoring</u> A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	√
S3.9.2	53.3.3	<u>Compliance of the Approved Measures and Auditing</u> Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	

### Annex G Implementation Schedule for Environmental Protection Measures (1 to 31 August 2017)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with			
		AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	<u>Archival Recording</u> An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of as- built drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	<u>General Construction Methods</u> Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F

	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S3.7.1 & 3.7.2		checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the cross referenced location plans and photo records. One set of updated CMP shall be submitted to the AMO for approval before	Whole site	During detailed design, construction, post- construction and operation	west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Landsca	ipe & Visi	ıal			
S4.7.27	-	<u>In-situ Tree Protection - Cordon Zone (CZ)</u> Cordon off each tree along its drip line (below the crown) with a chain- link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.	Whole site	During construction	<> The chain-link fencing for the retained trees has been removed to enable the laying of floor slab and repairing of the planters. A tree protection zone around the planter of each tree has been provided. Barricades are set up for Tree 6, 7, 8 and 9 and the barricaded zone is clear of construction materials or equipment. The vicinity of Tree 5 is also clear of construction materials or equipment. A temporary shelter has been erected around Tree 11. No major construction works in the vicinity of the trees or within the CPS site are being carried out.
S4.7.2	-	In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.	Whole site	During construction	N/A – no root pruning has been conducted yet
S4.7.2	-	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the	Whole site	During construction	N/A – The sprinkler cleansing system has been removed as major dust-generating works within the

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		tree or at a suitable location on an adjacent building to provide the means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			CPS site have been completed.
S4.7.2	S4	<u>In-situ Tree Protection - Monthly inspection</u> Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.	Whole site	During construction	$\checkmark$
S4.7.2	-	<u>Light Control</u> Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	$\checkmark$
S4.7.2	S4	<u>Compensatory Tree Planting</u> A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	√ - Planters of the compensatory trees are being built in the Parade Ground during the reporting period.

A Recommended Mitigation Measures	Location	When to Implement the Measure	Status
underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.			
Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements			
The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.			
<i>Existing Granite Revetment Wall</i> The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.	Inner Southern Wall	During detailed design and construction	$\checkmark$
New Custom Paving         New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	N/A – No custom paving was conducted during the reporting month.
In-situ Tree Protection - Quarterly inspection         Quarterly Inspection of affected and newly planted trees by an         experienced and appropriately trained arborist or horticulturist using         Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk         Assessment Form developed by Development Bureau         (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf)         or a form designed by a tree expert and approved by Tree Management	Whole site	During post construction and operation	N/A – The quarterly inspection will be conducted at later stage.
	underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.         Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements         The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department. <i>Existing Granite Reventent Wall</i> The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance. <i>New Custom Paving</i> New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces. <i>In-situ Tree Protection - Quarterly inspection</i> Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf)	underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.         Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements         The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.       Inner Southern Wall         Internet store face along the southern wall of the Site shall be preserved to its original historical appearance.       Whole site         New Custom Paving       Whole site         New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.       Whole site         Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf)	Implement the Measureunderneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation. Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirementsThe replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.Inner Southern WallDuring detailed design and construction <i>Existing Granite Revetment Wall</i> The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.Whole siteDuring detailed design and construction <i>New. Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.</i> Whole siteDuring post construction <i>In-situ Tree Protection - Quarterly inspection</i> quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 - Tree Group Inspection Form and Form 2 - Tree Risk Assessment Form developed by Development Bureau (http://towu.trees.gov.hk/en/doc/TRAGuideline_Jhy2010version_combine.pdf)Whole siteDuring post construction and operation

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
<i>S5.9</i>	-	<ul> <li>The following site practices should be followed during the construction of the Project:</li> <li>Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase;</li> <li>Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase;</li> <li>Mobile plant, if any, will be sited as far away from NSRs as possible;</li> <li>Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum;</li> <li>Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	Whole Site	During construction	
<i>S5.9</i>	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	$\checkmark$
<i>S5.9</i>	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m <sup>-2</sup> and have no openings or gaps.	Whole Site	During construction	√
<i>S5.9</i>	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	√
<i>S</i> 5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	$\checkmark$
Air Qu	ality				
S6.8.1	-	Dust control measures stipulated in the <i>Air Pollution Control</i> ( <i>Construction Dust</i> ) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	$\checkmark$
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	$\checkmark$
S6.8.1	-	along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if	Whole Site	During	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		required, from the ground floor level of building for construction of superstructure of the new buildings.		construction	
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	$\checkmark$
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A – Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	$\checkmark$
Water (	Quality	•			
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	$\checkmark$
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A – Not observed.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	$\checkmark$
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A – Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	$\checkmark$
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	$\checkmark$
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	$\checkmark$
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A – Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A – Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	$\checkmark$
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	$\checkmark$
Waste I	Manageme	nt			·
S8.5	S6.3.1 & Table 6.1	<u>General</u> The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	$\checkmark$
S8.5	-	<u>Management of Waste Disposal</u> The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		system will be included as one of the contractual requirements and implemented by the contractor.			
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	$\checkmark$
S8.5	S6.3	<u>Reduction of Construction Waste Generation</u> C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	$\checkmark$
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	$\checkmark$
S8.5	S6	<ul> <li>Containers used for storage of chemical waste shall:</li> <li>Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;</li> <li>Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and</li> <li>Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>.</li> </ul>	Whole Site	During construction and operation	$\checkmark$
S8.5	S6	<ul> <li>Storage areas for chemical waste shall:</li> <li>Be clearly labelled and used solely for the storage of chemical waste;</li> <li>Be enclosed on at least 3 sides;</li> <li>Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest;</li> <li>Have adequate ventilation;</li> <li>Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and</li> </ul>	Whole Site	During construction and operation	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		<ul> <li>Be arranged so that incompatible materials are appropriately separated.</li> </ul>			
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	$\checkmark$
S8.5	S6 & Table 6.1	<u>General Refuse</u> General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	√
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	$\checkmark$
S8.5	S6	<u>Staff Training</u> At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	$\checkmark$
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	$\checkmark$

Remark:

 $\sqrt{}$  Compliance of Mitigation Measures

<> Compliance of Mitigation but need improvement

x Non-compliance of Mitigation Measures

▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd

Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd

N/A Not Applicable in Reporting Period

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultur	al Heritag	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	$\checkmark$
S3.9.2	S3.3.1	<u>Vibration Monitoring</u> A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	√
\$3.9.2	S3.3.3	<u>Compliance of the Approved Measures and Auditing</u> Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	$\Leftrightarrow$

### Annex G Implementation Schedule for Environmental Protection Measures (1 to 30 September 2017)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with			
		AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	<u>Archival Recording</u> An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of as- built drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	<u>General Construction Methods</u> Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F

	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S3.7.1 & 3.7.2		checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the cr	Whole site	During detailed design, construction, post- construction and operation	west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Landsca	ipe & Visi	ıal			
S4.7.27	-	<u>In-situ Tree Protection - Cordon Zone (CZ)</u> Cordon off each tree along its drip line (below the crown) with a chain- link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.	Whole site	During construction	<> The chain-link fencing for the retained trees has been removed to enable the laying of floor slab and repairing of the planters. A tree protection zone around the planter of each tree has been provided. Barricades are set up for Tree 6, 7, 8 and 9 and the barricaded zone is clear of construction materials or equipment. The vicinity of Tree 5 is also clear of construction materials or equipment. A temporary shelter has been erected around Tree 11. No major construction works in the vicinity of the trees or within the CPS site are being carried out.
S4.7.2	-	In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.	Whole site	During construction	N/A – no root pruning has been conducted yet
S4.7.2	-	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the	Whole site	During construction	N/A – The sprinkler cleansing system has been removed as major dust-generating works within the

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		tree or at a suitable location on an adjacent building to provide the means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			CPS site have been completed.
S4.7.2	S4	<u>In-situ Tree Protection - Monthly inspection</u> Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.	Whole site	During construction	$\checkmark$
S4.7.2	-	<u>Light Control</u> Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	$\checkmark$
S4.7.2	S4	<u>Compensatory Tree Planting</u> A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	√ - Planters of the compensatory trees are being built in the Parade Ground during the reporting period.

M&A ef.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
	underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.			
	Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements			
	The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.			
Ł	<i>Existing Granite Revetment Wall</i> The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.	Inner Southern Wall	During detailed design and construction	$\checkmark$
	<u>New Custom Paving</u> New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	√
	<u>In-situ Tree Protection - Quarterly inspection</u> Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management	Whole site	During post construction and operation	N/A – The quarterly inspection will be conducted at later stage.
ef		<ul> <li>underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.</li> <li>Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements</li> <li>The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.</li> <li><i>Existing Granite Revetment Wall</i></li> <li>The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.</li> <li><i>New Custom Paving</i></li> <li>New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.</li> <li><i>In-situ Tree Protection - Quarterly inspection</i></li> <li>Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf)</li> </ul>	i.       underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.         Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements         The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.       Inner Southern Wall         The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.       Whole site         New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.       Whole site         Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Burreau (http://toww.trees.gov.hk/en/doc/TRAGuideline_July2010rersion_combine.pdf)	i.       Implement the Measure         i.       Implement the Measure         i.       Inderneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.         Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements         The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.       Inner Southern Wall       During detailed design and construction         The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.       Whole site       During detailed design and construction         New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.       Whole site       During post construction and operation and construction and construction and operation and form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.bk/m/doc/TRAGuideline_July2010version_combine.pdf)       Whole site       During post construction and operation and operation and construction and operation and construction and operation account of the could be preserved by Development Bureau (http://www.trees.gov.bk/m/doc/TRAGuideline_July2010version_combine.pdf)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
<i>S5.9</i>	-	<ul> <li>The following site practices should be followed during the construction of the Project:</li> <li>Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase;</li> <li>Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase;</li> <li>Mobile plant, if any, will be sited as far away from NSRs as possible;</li> <li>Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum;</li> <li>Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	Whole Site	During construction	√
<i>S5.9</i>	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	$\checkmark$
<i>S5.9</i>	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m <sup>-2</sup> and have no openings or gaps.	Whole Site	During construction	V
<i>S5.9</i>	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	$\checkmark$
<i>S</i> 5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	$\checkmark$
Air Qu	ality				
S6.8.1	-	Dust control measures stipulated in the <i>Air Pollution Control</i> ( <i>Construction Dust</i> ) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	$\checkmark$
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	$\checkmark$
S6.8.1	-	along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if	Whole Site	During	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		required, from the ground floor level of building for construction of superstructure of the new buildings.		construction	
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	$\checkmark$
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A – Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	$\checkmark$
Water (	Quality	•			
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	$\checkmark$
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A – Not observed.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	V
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A – Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	$\checkmark$
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	$\checkmark$
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	$\checkmark$
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A – Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A – Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	$\checkmark$
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	$\checkmark$
Waste I	Manageme	nt	·		·
S8.5	S6.3.1 & Table 6.1	<u>General</u> The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	$\checkmark$
S8.5	-	<u>Management of Waste Disposal</u> The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	$\checkmark$
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		system will be included as one of the contractual requirements and implemented by the contractor.			
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	$\checkmark$
S8.5	S6.3	<u>Reduction of Construction Waste Generation</u> C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	$\checkmark$
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	$\checkmark$
S8.5	S6	<ul> <li>Containers used for storage of chemical waste shall:</li> <li>Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;</li> <li>Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and</li> <li>Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>.</li> </ul>	Whole Site	During construction and operation	$\checkmark$
S8.5	S6	<ul> <li>Storage areas for chemical waste shall:</li> <li>Be clearly labelled and used solely for the storage of chemical waste;</li> <li>Be enclosed on at least 3 sides;</li> <li>Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest;</li> <li>Have adequate ventilation;</li> <li>Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and</li> </ul>	Whole Site	During construction and operation	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		• Be arranged so that incompatible materials are appropriately separated.			
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	$\checkmark$
S8.5	S6 & Table 6.1	<u>General Refuse</u> General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	$\checkmark$
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	$\checkmark$
S8.5	S6	<u>Staff Training</u> At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	√
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	$\checkmark$

Remark:

 $\sqrt{}$  Compliance of Mitigation Measures

<> Compliance of Mitigation but need improvement

x Non-compliance of Mitigation Measures

▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd

Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd

N/A Not Applicable in Reporting Period

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Cultur	al Heritag	ge			
S3.9.1	S3.2.6	Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO.	In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO	During detailed design and construction	
S3.9.2	S3.3.1	<u>Vibration Monitoring</u> A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works.	Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road)	During detailed design and construction	1
\$3.9.2	S3.3.3	<u>Compliance of the Approved Measures and Auditing</u> Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed	Whole site	Prior to and during construction	

# Annex G Implementation Schedule for Environmental Protection Measures (1 to 31 October 2017)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with			
		AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage.			
S3.9.3	S3.3.4	<u>Archival Recording</u> An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of as- built drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan.	Whole Site	During detailed design, construction and prior to operation	N/A – Archival recording will be conducted at later stage.
S3.7.3	-	<u>General Construction Methods</u> Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be	Whole site	During construction	At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F

	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S3.7.1 & 3.7.2		checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the cross referenced location plans and photo records. One set of updated CMP shall be submitted to the AMO for approval before	Whole site	During detailed design, construction, post- construction and operation	west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
Landsca	ipe & Visi	ıal			
S4.7.27	-	<u>In-situ Tree Protection - Cordon Zone (CZ)</u> Cordon off each tree along its drip line (below the crown) with a chain- link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ.	Whole site	During construction	<> The chain-link fencing for the retained trees has been removed to enable the laying of floor slab and repairing of the planters. A tree protection zone around the planter of each tree has been provided. Barricades are set up for Tree 6, 7, 8 and 9 and the barricaded zone is clear of construction materials or equipment. The vicinity of Tree 5 is also clear of construction materials or equipment. A temporary shelter has been erected around Tree 11. No major construction works in the vicinity of the trees or within the CPS site are being carried out.
S4.7.2	-	In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree.	Whole site	During construction	N/A – no root pruning has been conducted yet
S4.7.2	-	In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the	Whole site	During construction	N/A – The sprinkler cleansing system has been removed as major dust-generating works within the

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		tree or at a suitable location on an adjacent building to provide the means to wash the foliage of the accumulated dust when necessary, particularly in the dry season.			CPS site have been completed.
S4.7.2	S4	<u>In-situ Tree Protection - Monthly inspection</u> Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days.	Whole site	During construction	$\checkmark$
S4.7.2	-	<u>Light Control</u> Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs.	Whole site	During construction and operation	$\checkmark$
S4.7.2	S4	<u>Compensatory Tree Planting</u> A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil	At identified compensatory tree planting location at the Parade Ground	During detailed design and construction	√ - Planters of the compensatory trees are being built in the Parade Ground during the reporting period.

M&A ef.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
	underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.			
	Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements			
	The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.			
Ł	<i>Existing Granite Revetment Wall</i> The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.	Inner Southern Wall	During detailed design and construction	$\checkmark$
	<u>New Custom Paving</u> New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.	Whole site	During detailed design and construction	√
	<u>In-situ Tree Protection - Quarterly inspection</u> Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management	Whole site	During post construction and operation	N/A – The quarterly inspection will be conducted at later stage.
ef		<ul> <li>underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.</li> <li>Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements</li> <li>The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.</li> <li><i>Existing Granite Revetment Wall</i></li> <li>The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.</li> <li><i>New Custom Paving</i></li> <li>New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.</li> <li><i>In-situ Tree Protection - Quarterly inspection</i></li> <li>Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf)</li> </ul>	i.       underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.         Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements         The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.       Inner Southern Wall         The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.       Whole site         New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.       Whole site         Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Burreau (http://toww.trees.gov.hk/en/doc/TRAGuideline_July2010rersion_combine.pdf)	i.       Implement the Measure         i.       Implement the Measure         i.       Inderneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation.         Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements         The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department.       Inner Southern Wall       During detailed design and construction         The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance.       Whole site       During detailed design and construction         New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces.       Whole site       During post construction and operation and construction and construction and operation and form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.bk/m/doc/TRAGuideline_July2010version_combine.pdf)       Whole site       During post construction and operation and operation and construction and operation and construction and operation account of the could be preserved by Development Bureau (http://www.trees.gov.bk/m/doc/TRAGuideline_July2010version_combine.pdf)

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
<i>S5.9</i>	-	<ul> <li>The following site practices should be followed during the construction of the Project:</li> <li>Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase;</li> <li>Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase;</li> <li>Mobile plant, if any, will be sited as far away from NSRs as possible;</li> <li>Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum;</li> <li>Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and</li> <li>Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	Whole Site	During construction	√
<i>S5.9</i>	-	Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints.	Whole Site	During construction	$\checkmark$
<i>S5.9</i>	-	Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m <sup>-2</sup> and have no openings or gaps.	Whole Site	During construction	V
<i>S5.9</i>	-	Use quiet PME as far as practicable to mitigate the construction noise impact.	Whole Site	During construction	$\checkmark$
<i>S</i> 5.9	-	Scheduling of construction activities with identified grouping of PMEs.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S5.11	S5	Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage.	Whole Site	During construction	$\checkmark$
Air Qu	ality				
S6.8.1	-	Dust control measures stipulated in the <i>Air Pollution Control</i> ( <i>Construction Dust</i> ) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions.	Whole Site	During construction	$\checkmark$
S6.8.1	-	In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Impervious sheet will be provided for skip hoist for material transport.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Vehicle washing facilities will be provided at the designated vehicle exit points.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Road sections between vehicle-wash areas and vehicular entrances will be paved.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles.	Whole Site	During construction	$\checkmark$
S6.8.1	-	along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides.	Whole Site	During construction	
S6.8.1	-	An effective dust screen will be provided to enclose scaffolding, if	Whole Site	During	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		required, from the ground floor level of building for construction of superstructure of the new buildings.		construction	
S6.8.1	-	Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity.	Area for Demolition Work	During construction	$\checkmark$
S6.8.1	-	ULSD will be used for all construction plant on-site.	Whole Site	During construction	$\checkmark$
S6.8.1	-	The engine of the construction equipment or trucks during idling will be switched off.	Whole Site	During construction	$\checkmark$
S6.8.1	-	Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions.	Whole Site	During construction	N/A – Not observed.
S6.10	S3.2	Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period.	Whole Site	During construction	$\checkmark$
Water (	Quality	•			
S7.6	-	Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly.	Whole Site	During construction	$\checkmark$
S7.6	-	All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of.	Whole Site	During construction	N/A – Not observed.

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system.	Whole Site	During construction	V
S7.6	-	Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events.	Whole Site	During construction	N/A – Not observed.
S7.6	-	All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal.	Whole Site	During construction	N/A – Not observed.
S7.6	-	Waste streams classifiable as chemical wastes will be properly stored, collected and treated.	Whole Site	During construction	$\checkmark$
S7.6	-	All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas.	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
S7.6	-	The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters.	Whole Site	During construction	$\checkmark$
S7.6	-	The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals.	Whole Site	During construction	$\checkmark$
S7.6	-	Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system	Whole Site	During construction	N/A – Not observed.
S7.6	-	The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable.	Whole Site	During construction	N/A – Not observed.
S7.6	-	The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer.	Whole Site	During construction	$\checkmark$
S7.8	S5.2	Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem.	Whole Site	During construction	$\checkmark$
Waste I	Manageme	nt	·		·
S8.5	S6.3.1 & Table 6.1	<u>General</u> The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works.	Whole Site	During construction	$\checkmark$
S8.5	-	<u>Management of Waste Disposal</u> The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer.	Whole Site	During construction	$\checkmark$
S8.5	S6.2	A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket	Whole Site	During construction	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		system will be included as one of the contractual requirements and implemented by the contractor.			
S8.5	S6 & Table 6.1	A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase.	Whole Site	During construction	$\checkmark$
S8.5	S6.3	<u>Reduction of Construction Waste Generation</u> C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	Whole Site	During construction	$\checkmark$
S8.5	S6	<u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD.	Whole Site	During construction and operation	$\checkmark$
S8.5	S6	<ul> <li>Containers used for storage of chemical waste shall:</li> <li>Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed;</li> <li>Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and</li> <li>Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>.</li> </ul>	Whole Site	During construction and operation	$\checkmark$
S8.5	S6	<ul> <li>Storage areas for chemical waste shall:</li> <li>Be clearly labelled and used solely for the storage of chemical waste;</li> <li>Be enclosed on at least 3 sides;</li> <li>Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest;</li> <li>Have adequate ventilation;</li> <li>Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and</li> </ul>	Whole Site	During construction and operation	$\checkmark$

EIA Ref.	EM&A Ref.	Recommended Mitigation Measures	Location	When to Implement the Measure	Status
		• Be arranged so that incompatible materials are appropriately separated.			
S8.5	S6	A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility.	Chemical Waste Treatment Centre at Tsing Yi	During construction and operation	$\checkmark$
S8.5	S6 & Table 6.1	<u>General Refuse</u> General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	Whole site	During construction	$\checkmark$
S8.5	S6	Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling.	Whole site	During construction and operation	$\checkmark$
S8.5	S6	<u>Staff Training</u> At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling.	Whole site	Commencement of construction	√
S8.7	S6.1 & 6.3	Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	Whole site	During construction	$\checkmark$

Remark:

 $\sqrt{}$  Compliance of Mitigation Measures

<> Compliance of Mitigation but need improvement

x Non-compliance of Mitigation Measures

▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd

Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd

N/A Not Applicable in Reporting Period

Annex H

Noise Monitoring Results

### Annex H Noise Monitoring Results

#### Daytime Noise Monitoring Results

### NM6 Chancery Mansion

Date	Start Time	End Time	Weather	Noise	level (dB(A)	), 30 min	Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90		Observed				
03-Aug-17	9:50	10:20	Cloudy	66.3	67.8	63.7	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
09-Aug-17	8:43	9:13	Sunny	65.7	67.1	63.4	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
15-Aug-17	15:00	15:30	Sunny	66.0	67.8	63.2	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
21-Aug-17	11:12	11:42	Sunny	62.1	63.2	61.3	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
25-Aug-17	14:35	15:05	Sunny	63.8	65.5	62.1	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
31-Aug-17	8:22	8:52	Sunny	63.5	64.9	61.8	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	62.1								
			Max.	66.3								

#### NM2 Ho Fook Building

				Noise	level (dB(A)	), 30 min	Major Construction Noise	Other Noise		Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Source(s) Observed	Source(s) Observed	Remarks	(m/s)	Model / ID	Model / ID
03-Aug-17	10:30	11:00	Cloudy	67.8	69.5	64.8	Interior fitting (within the project site)	Traffic noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
09-Aug-17	10:40	11:10	Sunny	68.9	71.1	65.8	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
15-Aug-17	14:20	14:50	Sunny	69.1	70.9	65.8	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
21-Aug-17	9:12	9:42	Sunny	66.1	68.0	62.7	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
25-Aug-17	15:48	16:18	Sunny	65.5	68.1	62.7	Interior fitting (within the project site)	Traffic Noise	-	0.4	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
31-Aug-17	10:16	10:46	Sunny	65.6	66.9	63.0	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	65.5								
			Max.	69.1								

### Annex H Noise Monitoring Results

### Daytime Noise Monitoring Results

### NM6 Chancery Mansion

Date	Start Time	End Time	Weather	Noise level (dB(A)), 30 min			Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID
				Leq	L10	L90	000100(0) 00001100	Observed		(		
06-Sep-17	14:40	15:10	Sunny	64.0	65.4	62.4	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
12-Sep-17	9:12	9:42	Sunny	63.6	65.1	62.2	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
18-Sep-17	9:50	10:20	Sunny	65.4	67.1	63.1	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
22-Sep-17	9:50	10:20	Sunny	63.7	65.0	61.5	Interior fitting (within the project site)	Traffic Noise	-	0.4	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
28-Sep-17	9:30	10:00	Sunny	63.6	65.2	61.9	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	63.6								
			Max.	65.4								

#### NM2 Ho Fook Building

				Noise	level (dB(A)	), 30 min	Major Construction Noise	Other Noise		Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Source(s) Observed	Source(s) Observed	Remarks	(m/s)	Model / ID	Model / ID
06-Sep-17	15:30	16:00	Sunny	67.0	68.1	64.3	Interior fitting (within the project site)	Traffic noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
12-Sep-17	14:40	15:10	Sunny	69.4	71.7	65.7	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
18-Sep-17	10:28	10:58	Sunny	69.0	71.0	65.0	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
22-Sep-17	10:28	10:58	Sunny	67.4	69.3	64.1	Interior fitting (within the project site)	Traffic Noise	-	0.3	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
28-Sep-17	10:09	10:39	Sunny	69.8	72.6	65.5	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	67.0								
			Max.	69.8								

### Annex H Noise Monitoring Results


#### Daytime Noise Monitoring Results

### NM6 Chancery Mansion

Date	Start Time	Start lime End lime Weather		level (dB(A)	), 30 min	Major Construction Noise Source(s) Observed	Other Noise Source(s)	Remarks	Wind Speed (m/s)	Noise Meter Model / ID	Calibrator Model / ID	
				Leq	L10	L90		Observed				
03-Oct-17	14:25	14:55	Sunny	63.3	65.3	61.4	Interior fitting (within the project site)	Traffic Noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
09-Oct-17	8:52	9:22	Cloudy	62.6	64.3	60.9	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
13-Oct-17	8:40	9:10	Sunny	62.9	64.4	60.7	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
19-Oct-17	8:50	9:20	Fine	64.4	65.9	62.2	Interior fitting (within the project site)	Traffic Noise	-	1.0	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
25-Oct-17	9:17	9:47	Sunny	65.3	67.6	62.2	Interior fitting (within the project site)	Traffic Noise	-	1.0	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
31-Oct-17	8:42	9:12	Sunny	62.6	64.3	60.2	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)
			Min.	62.6								
			Max.	65.3								

#### NM2 Ho Fook Building

		End Time		Noise	level (dB(A)	), 30 min	Major Construction Noise	Other Noise		Wind Speed	Noise Meter	Calibrator	
Date	Start Time	End Time	Weather	Leq	L10	L90	Source(s) Observed	Source(s) Observed	Remarks	(m/s)	Model / ID	Model / ID	
03-Oct-17	15:03	15:33	Sunny	69.1	71.7	63.6	Interior fitting (within the project site)	Traffic noise	-	0.2	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
09-Oct-17	10:57	11:27	Cloudy	66.2	67.8	62.9	Interior fitting (within the project site)	Traffic Noise	-	0.5	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
13-Oct-17	9:17	9:47	Sunny	65.9	67.9	63.1	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
19-Oct-17	9:28	9:58	Fine	68.1	69.7	63.9	Interior fitting (within the project site)	Traffic Noise	-	1.0	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
25-Oct-17	9:55	10:25	Sunny	67.9	70.9	64.4	Interior fitting (within the project site)	Traffic Noise	-	0.8	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
31-Oct-17	9:20	9:50	Sunny	66.9	68.4	63.8	Interior fitting (within the project site)	Traffic Noise	-	1.0	CEL-633A (S/N 3521757)	CEL-120 (S/N 3421612)	
			Min.	65.9					•				
			Max.	69.1									

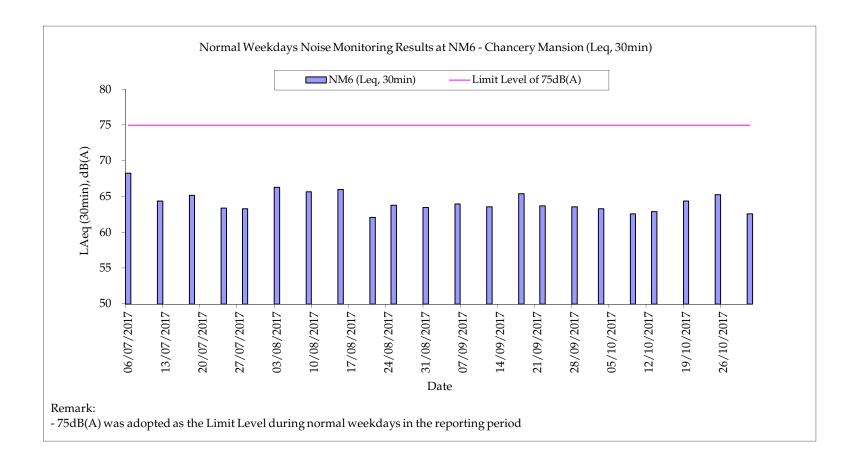



Annex I

Construction Programme for the Project


Activity	Activity	Orig	Start	Finish				2017					2018	
		Dur	Date	Date	M APR	MAY	JUN	JUL AUG	SEP	OCT NOV	DEC	JAN	FEB	MAR
CENTRAL POL														
													1	
SB01-0010	BLOCK 1 - FACADE WORK	_		06FEB17A									1	
SB01-0020	BLOCK 1 - FINISHES & E/M INCL TEMP SITE OFFICE	384*	21JUL16A	08AUG17				BLOCK	K 1 - FINISHES & E/M	NCL TEMP SITE OFFICE			   	
BLOCK 2 - ARMO														
SB02-0010	BLOCK 2 - FACADE WORK	_		25NOV16A									1	
SB02-0020	BLOCK 2 - FINISHES & E/M WORK	245*	21JUL16A	22MAR17A				 						
BLOCK 3 - BARF	RACK BLOCK			1										
SB03-0010	BLOCK 3 - FACADE WORK			27MAY17		BI	LOCK 3 - FACADE						- 	
SB03-0020	BLOCK 3 - FINISHES, E/M WORK & PART FLOOR STRAP	229*	05DEC16A	21JUL17				BLOCK 3 - FINIS	SHES, E/M WORK & P/					
SB03-0030	BLOCK 3 - 2/F FLOOR STRAP	73*	05AUG17	16OCT17			 			BLOCK 3 - 2/F FLOOR ST	RAP(AFTER O	P)		
BLOCK 6 - DORM	MITORY BLOCK C			T										
SB06-0010	BLOCK 6 - FACADE WORK	33*	01NOV16A	03DEC16A									1   	
SB06-0020	BLOCK 6 - FINISHES & E/M WORK	302*	09AUG16A	06JUN17			BLOCK 6 - FINI	SHES & E/M WORK					1	
BLOCK 7 - DORM	MITORY BLOCK D												1   	
SB07-0010	BLOCK 7 - FINISHES & E/M WORK	302*	09AUG16A	06JUN17			BLOCK 7 - FINI	SHES & E/M WORK						
BLOCK 8 - ABLU	ITIONS BLOCK													
SB08-0010	BLOCK 8 - FACADE WORK	178*	24NOV16A	20MAY17		BLOC	K 8 - FACADE WOI	RK						
SB08-0020	BLOCK 8 - FINISHES & E/M WORK	270*	07OCT16A	03JUL17			E	BLOCK 8 - FINISHES & E/	M WORK					
BLOCK 9 - CENT	RAL MAGISTRACY					1	   						1	   
SB09-0010	BLOCK 9 - FACADE WORK INCL SOUTH ELEVATION	406*	25AUG16A	04OCT17						BLOCK 9 - FACADE WORK INCL	SOUTH ELEV	ATION		
SB09-0020	BLOCK 9 - FINISHES & E/M WORK	401*	25AUG16A	29SEP17			 	 		BLOCK 9 - FINISHES & E/M WORK			-   	1
SB09-0030	BLK 9-COURT RM/ CANOPY STRENGTHEN &REINSTATEMENT	223*	26MAY17	03JAN18				~~~~~	****		*****	BLK 9-COURT	RM/ CANOPY	STRENGTHEN &F
BLOCK 10 - SUP	ERINTENDENTS HOUSE						   	I					   	
SB10-0010	BLOCK 10 - FACADE WORK INCL BALCONY REPAIR	398*	06OCT16A	07NOV17						BLOCK 10 - F	ACADE WORK	INCL BALCONY	REPAIR	
SB10-0020	BLOCK 10 - FINISHES & E/M WORK INCL FLOOR STRAP	387*	04OCT16A	250CT17						BLOCK 10 - FINISHE	S & E/M WORI	K INCL FLOOR S	TRAP	1
BLOCK 11 - A HA		1 1					l						   	
SB11-0010	BLOCK 11 - FACADE WORK	219*	07OCT16A	13MAY17		BLOCK 1	1 - FACADE WORK						1	
SB11-0020	BLOCK 11 - FINISHES & E/M WORK			14JUL17			<u> </u>	BLOCK 11 - FINISHE	ES & E/M WORK				 	1
BLOCK 12 - B H														
SB12-0010	BLOCK 12 - FACADE WORK	376*	14JUL16A	24JUL17				BLOCK 12 - FA	ACADE WORK					
SB12-0020	BLOCK 12 - FINISHES & E/M WORK	365*		13JUL17				BLOCK 12 - FINISHE	S & E/M WORK				1	
BLOCK 13 - C H						1	l	I					1	
SB13-0010	BLOCK 13 - FACADE WORK INCL CANOPY REMOVAL	257*	06OCT16A	19JUN17			BLOCK	13 - FACADE WORK INCL	CANOPY REMOVAL				1	
SB13-0020	BLOCK 13 - FINISHES & E/M WORK	_	060CT16A				BLOC	K 13 - FINISHES & E/M W	/ORK				i I I	1
BLOCK 14 - D H		202	00001104	24001117										
SB14-0010	BLOCK 14 - FACADE WORK	281*	21SEP16A	28 II IN17			BLO	OCK 14 - FACADE WORK					1	
SB14-0020	BLOCK 14 - FINISHES & E/M WORK INC CROSS BRACING		21SEP16A			1		BLOCK 14 - FINISHES 8		SS BRACING				
BLOCK 15 - E HA		290	LIGEFIOA	0/00L1/									I	
SB15-0010	BLOCK 15 - FACADE WORK	2/1/*	04.11.11.164	04MAR17A									1	
SB15-0010	BLOCK 15 - FINISHES & E/M WORK	_	04JUL16A					K 15 - FINISHES & E/M W	/ORK				 	
		330	04JUL16A	24JUN1/									 	
BLOCK 17 - F HA	BLOCK 17 - FACADE WORK INC EXT WINDOW TOP RAIL	210*	21JUL16A	26MAV17		RI		WORK INC EXT WINDOW					 	
								17 - FINISHES & E/M WO						
SB17-0020	BLOCK 17 - FINISHES & E/M WORK	335*	21JUL16A	20JUN17			BLOUK						 	
	BLOCK 19 - BAUHINIA HOUSE           SB19-0010         BLOCK 19 - FINISHES & E/M WORK         195*         11NOV16A         24MAY17         BLOCK 19 - FINISHES & E/M WORK													
SB19-0010	BLOCK 19 - FINISHES & E/M WORK	195*	11NOV16A	24MAY17					 				 	
BLOCK 50 OLD I			00 11 11 1 1	001115-15					FINISHES & E/M WOR					
SB50-0010	OBW FINISHES & E/M WORK INC R54	416*	20JUN16A	09AUG17		i		OBM					1	
Start Date Finish Date	07JUL10 09AUG18		Early Bar	7D02     CENTRAL POLICE STATION     Sheet 1 of 2       GCL/P/J3416/SUM       Date     Revision			ookod Annus							
Data Date	27APR17		Progress Bar		CONS	ERVATION AN	D REVITALIZA	TION		_	Date	Revision	Ch	ecked Approved
Run Date	04MAY17 13:04					ROGRAMME			香港賽馬和					
				5		EXCL BL			Jockey Club	🖥 🔚 Gammor	า 🥅			
	(WITH PROGRESS AS OF 27 APRIL 2017)													
?Primavera Systems, Inc.														

Activity Orig Start Finish										2017		2018					
ID	Description	Dur	Date	Date	M APF	2	MAY	JUN	JUL	AUG	SEP	ОСТ	NOV	DEC	JAN	FEB	MAR
BLOCK 51 ARE	BUTHNOT WING									I I	1		1	l l		1	1
SB51-0010	AW - FINISHES & E/M WORK	379*	20JUN16A	03JUL17					AW - FINISHES	S & E/M WORK							
EXTERNAL WO	DRKS	i				1				l l	1					1	
SBEW-0010	EXTERNAL WORK (INCL BLK 4 PROTECTIVE PLATFORM)	543*	04JUL16A	28DEC17									- -		EXTERNAL WOR	K (INCL BLK 4	PROTECTIVE
STATUTORY IN	ISPECT & HANDOVER (EXCL BLK 09 & 10)	I								1						1	
SBST-0010	SUBMIT BA13 & BA14	0		21JUL17					♦SU	BMIT BA13 & BA	14					1	
SBST-0020	BD INSPECTION	14*	22JUL17	04AUG17						BD INSPECTI	ON						
SBST-0030	ISSUE OP & BA14 ACKNOWLEDGEMENT	0		04AUG17						ISSUE OP &	BA14 ACKNO	DWLEDGEMENT					
SBST-0040	HANDOVER FOR PC	27*	22JUL17	17AUG17						HAND	OVER FOR P	c					
SBST-0050	PRACTICAL COMPLETION	0		17AUG17						PRAC	CTICAL COM	PLETION					
STATUTORY IN	ISPECTIONS & HANDOVER (BLK 10)		1	1						   	1		i İ İ			1	
SBST-0170	SUBMIT BA14	0		03NOV17									SUBMIT B	BA14			
SBST-0180	BD INSPECTION	28*	04NOV17	01DEC17						l I				BD INSPECTIO	N		
SBST-0190	ISSUE BA14 ACKNOWLEDGEMENT	0		01DEC17										ISSUE BA14		MENT	
SBST-0200	HANDOVER FOR PC	28*	04NOV17	01DEC17						l l	l l				DR PC	i I	
SBST-0210	PRACTICAL COMPLETION	0		01DEC17											OMPLETION		
STATUTORY IN	ISPECTIONS & HANDOVER (BLK 9)			I							1					1	1
SBST-0110	SUBMIT BA14	0		14DEC17						   	1		1	♦SUBM	T BA14	1   	
SBST-0120	BD INSPECTION	28*	15DEC17	11JAN18											BD INSPE	CTION	
SBST-0130	ISSUE BA14 ACKNOWLEDGEMENT	0		11JAN18	1					1	1		1		<b>ISSUE B</b>	A14 ACKNOW	LEDGEMENT
SBST-0140	HANDOVER FOR PC	28*	15DEC17	11JAN18	1										HANDOVE	R FOR PC	
SBST-0150	PRACTICAL COMPLETION	0		11JAN18	1					1	1		1	i I	PRACTIC	CAL COMPLET	ION

Start Date	07JUL10	Early Bar	7D02 CENTRAL POLICE STATION Sheet 2 of 2	2		GCL/P/J3416/SUM/	CP07B	
Finish Date	09AUG18				Date	Revision	Checked	Approved
Data Date	27APR17	Progress Bar	CONSERVATION AND REVITALIZATION					
Run Date	04MAY17 13:04			香港賽馬會				
			SUMMARY PROGRAMME TO COMPLETION REV 7B	C The Hong Kong				
			(EXCL BLOCK 4)	Jockey Club Gammon				
			(EXCL BLOCK 4)					
			(WITH PROGRESS AS OF 27 APRIL 2017)					
	?Primavera Systems, Inc.							

	Activity Description	Dur	Start Date	Finish Date	SA Programme Start	SA Programme Finish	% Comp	Last Update 30MARCH2017 % Comp	2016         Second	S O N
ΔΝΔGEMENT (	CONTRACT / ON-SITE WORKS				Start	FINISH		% Comp		····
ITE WORKS										
Proposed New Fo	potbridge									
	rdige Piling & Pile Cap									
	Footbridge const'n - piling, ELS & pile cap	630*	05OCT15A	25JUN17	26JUL15	20JUL16	91	86	Footbridge const'n - piling, ELS & pile cap	
F2300125 S	STAGE 1 - PILING & PILE TEST	583*	05OCT15A	09MAY17	26JUL15	17APR16	98	91	STAGE 1 - PILING & PILE TEST	
F2300135 S	STAGE 2 - PILE CAP CONSTRUCTION	40*	10MAY17	18JUN17	18APR16	01JUN16	0	0	STAGE 2 - PILE CAP CONSTRUCTION	
F2300145 S	STAGE 3 - ROADWORK REINSTATEMENT	7*	19JUN17	25JUN17	02JUN16	20JUL16	0	0		
WP402 - Foorbrid	idge Superstructure									
	Footbridge cont'n - site access	0	26JUN17		21JUL16		0	0	Footbridge cont'n - site access	
F2300110 F	Footbridge cont'n-Pier, bridge deck&Finish/E&M	223*	26JUN17	03FEB18	21JUL16	26APR17	0	0	Footbridge cont'n-Pier, bridge deck&	Finish/E&M
	Footbridge con'tn - Pier & bridge deck structure	130*		02NOV17	21JUL16	27NOV16	0	0	Footbridge con'tn - Pier & bridge deck structure	i i
	Footbridge cont'n - Finishes & E/M & inspection	93*		03FEB18	28NOV16	26APR17	0	0	Footbridge cont'n - Finishes & E/M &	inspection
	ontractors Procurement	1.50					J			• •
	Superstruct WP - Mobilise/Lead time to commence	150	17MAR16A	20MAY17	30DEC15	27MAY16	84	65	Superstruct WP - Mobilise/Lead time to commence	
BD Submission a										
1	Superstructure	60	22MAR17A	20MAY17			60	13	Superstructure	
Construction - Fe		00				<u> </u>	00	10		
Load Test - Shear										
	BA10 Notice Period Completed for ELS	0		16MAR17A			100	100	◆BA10 Notice Period Completed for ELS	
	GEO comment- additional monitoring point	0		22MAR17A			100		GEO comment- additional monitoring point	
	GEO comment- pile load test requirements	0		28MAR17A			100		GEO comment- pile load test requirements	
	· · ·	-							Planking suspended after GEO visit on 310CT2016	
	Planking suspended after GEO visit on 310CT2016	0		310CT16A			100			
	Explore alternative ELS / planking method	17	01NOV16A				100		Explore alternative ELS / planking method	
	Resubmit ELS/planking drawing to BD for approval	30	25NOV16A				100	100	Resubmit ELS/planking drawing to BD for approval (withdrew on 16Dec2016)	1
	Withdraw ELS/planking BD resubmisstion	0		16DEC16A			100	100	Withdraw ELS/planking BD/resubmisstion	
	Prepare & submit test report - shear H pile	11	14APR17A		05FEB16	18FEB16	100	0	Prepare & submit test report - shear H pile	
F2302160 S	Submit BA8 for ELS consent	28	15FEB17A	14MAR17A			100	100	Submit BA8 for ELS consent	
General		-	-1			1				
	BD acknowledgement	28	11APR17A	09MAY17	21MAR16	17APR16	54	0	BD acknowledgement	
F2302090 A	Apply pile cap consent	28	11APR17A	09MAY17	21MAR16	17APR16	54	0	Apply pile cap consent	
F2302110 A	Apply superstructure consent	30	21MAY17	19JUN17	23JUN16	13JUL16	0	0	Apply superstructure consent	
<b>Construction - S</b>	Structure, Finishes & E/M									1
F2302094 E	Exc pile caps (zone A) Part 1	46	12DEC16A	05JAN17A			100	100	Exc pile caps (zone A) Part 1	
F2302094C E	Exc pile cap (zone A) Part 2	20	21FEB17A	07MAR17A			100	100	Exc pile cap (zone A) Part 2	
F2302100 C	Construct pile cap	40	10MAY17	18JUN17	18APR16	01JUN16	0	0	Construct pile cap	
F2302120 E	Backfilling of excavated area	7	19JUN17	25JUN17	14JUL16	20JUL16	0	0	Backfilling of excavated area	1
F2302130 E	Erection of temporary steel decking	70	26JUN17	03SEP17	21JUL16	28SEP16	0	0	Erection of temporary steel decking	l I
F2302200 F	Pier Construction	56		03SEP17	04AUG16	28SEP16	0	0		
	Footbridge Structure	60		02NOV17	29SEP16	27NOV16	0	0		
	Ex Central escalator modification work	45		180CT17	1002.10		0	0		
	Finishes & E&M	58		30DEC17	28NOV16	25FEB17		0	Finishes & E&M(assume no needle gun fini	ishes)
					20110110	2JFED1/		0		
	Curing	28		30NOV17	0005010	0414117	0	0		
	Dismantle of temporary steel decking	30		30DEC17	26DEC16	24JAN17	0	0	Dismantle of temporary steel decking	
	Footpath refurbishment work	30	16DEC17	14JAN18	10JAN17	08FEB17	0	0	Footpath refurbishment work	
	Statutory Inspection	35		03FEB18	26FEB17	26APR17	0	0		- I - I - I - I - I - I - I - I - I - I
	Remaining roadworks at street level	30	15JAN18	13FEB18			0	0	Remaining roadworks at street leve	el l

Data Date Run Date



TARGET CONSTRUCTION PROGRAMME FOR FOOTBRIDGE (WITH PROGRESS AS OF 27 APR 2017) (WITH OBJECTION FROM PUBLIC)



?Primavera Systems, Inc.

Annex J

Waste Flow Table

## Annex J – Waste Flow Table

	C&D Materials	Number of Trucks	Volume of C&D	C&D Materials	Number of Trucks for	Volume of C&D		Chemical	Recycled materials			
	(inert) (tonnes) <sup>(a)</sup>	for C&D Materials Disposal (inert)			C&D Materials Disposal (non-inert)	Materials (non- inert) (m <sup>3</sup> ) <sup>(c)</sup>			Paper/cardboard (kg)	Plastics (kg)	Metals (kg	
										Ŭ		
October 2011 – ovember 2011	_	_	_									
ecember-11	0	0	0	33.5 18.25	12 6	58.50 29.25	0	0	38 112	6 0	36423 24000	
inuary-12	354.14	40	195.00	16.88	5	29.25	2400	0	0	0	3820	
bruary-12	252.35	15	73.13	17.13	5	24.38	1400	0	223	0	8910	
larch-12	666.43	62	302.25	28.56	9	43.88	3200	0	0	0	48490	
pril-12	688.68	72	351.00	17.54	5	24.38	0	0	0	0	124030	
ay-12	492.33	61	297.38	36.33	13	63.38	0	0	266	0	0	
ne-12	383.11	45	219.38	27.41	8	39.00	40	45	0	0	1100	
ly-12	217.98	25	121.88	23.22	8	39.00	0	0	302	0	1750	
ugust-12	341.87	42	204.75	48.87	16	78.00	0	0	0	0	2310	
ptember-12	227.7	29	141.38	37.99	12	58.50	0	0	383	0	1410	
ctober-12	290.58	44	214.50	30.34	8	39.00	0	0	86	0	3150	
ovember-12	843.86	100	487.50	47.44	15	73.13	0	0	0	0	5650	
ecember-12	207.5	27	131.63	88.66	28	136.50	0	0	0	0	27230	
nuary-13	273.64	34	165.75	276.17	74	360.75	0	0	172	0	8120	
bruary-13	945.97	131	638.63	177.54	46	224.25	0	0	0	0	1080	
arch-13	1236.96	151	736.13	230.55	60	292.50	0	0	164	0	11300	
pril-13	1406.79	187	911.63	232.27	63	307.13	135	12	225	0	21220	
ay-13	2679.91	317	1545.38	176.68	44	214.50	0	0	62	0	17286	
ne-13	3062.38	356	1735.50	212.63	56	273.00	0	0	0	0	7150	
ly-13	3814.86	465	2266.88	114.36	43	209.63	0	0	168	0	14843	
ugust-13	2831.78	353	1720.88	89.23	25	121.88	0	0	0	0	7190	
ptember-13	979.49	141	687.38	103.73	29	141.38	40	0	0	0	4030	
ctober-13	2170.54	270	1316.25	157.48	41	199.88	135	0	0	0	3120	
ovember-13	836.74	109	531.38	191.58	44	214.50	0	0	202	0	18486	
ecember-13	2606.76	296	1443.00	192.54	49	238.88	0	0	0	0	10100	
nuary-14	3813.53	400	1950.00	97.87	36	175.50	0	Ő	0	0	14110	
bruary-14	3378.16	316	1540.50	37.84	14	68.25	0	0	0	0	9800	
arch-14	5256.15	516	2515.50	89.39	31	151.13	0	0	6000	0	19030	
oril-14	3006	299	1457.63	114.31	33	160.88	45	0	0	0	6950	
ay-14	3195.53	310	1511.25	119.54	37	180.38	4.5	0	0	0	7000	
ne-14	2176.81	205	999.38	148.8	45	219.38	0	0	242	0	8830	
ly-14	1009.96	111	541.13	147.36	49	238.88	0	0	0	0	6680	
ugust-14	379.23	53	258.38	211.86	47	229.13	0	0	0	0	13690	
ptember-14	1216.97	123	599.63	264.83	56	273.00	0	0	0	0	9720	
ctober-14	1162.34	123	604.50	294.33	65	316.88	0	0	0	0	57080	
ovember-14	1249.55	124	687.38	336.57	75	365.63	0	0	0	0	6660	
ecember-14	1177.63	141 129	628.88	260.33	69		0	0	68	0	12080	
		69	336.38	200.33	58	336.38	0		0	0	3000	
nuary-15	614.34					282.75		0		0		
bruary-15	593.97	78	380.25	133.74	40	195.00	0	0	0 106	0	5420	
arch-15	766.35	93	453.38	245.77	71	346.13					8980	
oril-15	594.77	78	380.25	195.55	51	248.63	0	0	0	0	3370	
ay-15	832.50	110	536.25	212.04	63	307.13	0	0	133		5090	
ne-15	673.87	84	409.50	222.66	72	351.00	0	0	23	0	0	
ly-15	1133.90	137	667.88	184.02	62	302.25	0	0	0	0	6950	
igust-15	1394.20	157	765.38	226.04	81	394.88	0	0	0	0	0	
ptember-15	942.39	107	521.63	330.23	108	526.50	0	0	0	0	0	
tober-15	1874.26	220	1072.50	286.27	109	531.38	0	0	60	0	0	
ovember-15	830.67	93	453.38	321.6	117	570.38	0	0	86	0	4970	
cember-15	596.00	58	282.75	250.51	107	521.63	0	0	103	0	16770	
nuary-16	505.11	57	277.88	265.56	120	585.00	0	0	0	0	6340	
bruary-16	274.16	30	146.25	128.66	70	341.25	0	0	170	0	0	
arch-16	114.67	17	82.88	380.06	116	565.50	0	0	0	0	0	
oril-16	244.83	34	165.75	308.28	113	550.88	0	0	0	0	0	
ay-16	402.49	55	268.13	216.79	74	360.75	0	0	0	0	0	
ne-16	173.01	20	97.50	109.25	36	175.50	0	0	248	0	0	
ly-16	303.68	37	180.38	83.99	40	195.00	0	0	0	0	0	
ıgust-16	147.28	19	92.63	112.63	46	224.25	0	0	0	0	0	
otember-16	17.64	3	14.63	88.26	39	190.13	0	0	226	0	0	
tober-16	57.59	9	43.88	69.64	28	136.50	0	0	0	0	0	
vember-16	14.21	2	9.75	105.39	33	160.88	0	0	0	0	0	
cember-16	29.61	4	19.50	69.45	27	131.63	0	0	260	0	0	
uary-17	27.51	4	19.50	51.97	22	107.25	0	0	190	0	0	
bruary-17	60.97	9	43.88	43.89	15	73.13	0	0	210	0	0	
arch-17	135.47	17	82.88	93.05	27	131.63	0	0	160	0	0	
oril-17	32.19	4	19.50	103.21	28	136.50	0	0	0	0	0	
ay-17	54.34	8	39.00	87.19	26	126.75	0	0	228	0	0	
ne-17	134.59	15	73.13	80.65	30	146.25	0	0	266	0	0	
y-17	12.61	1	4.88	57.54	24	146.25	0	0	0	0	0	
igust-17	79.39	10	48.75	58.03	24 24	117.00	0	0	0	0	0	
ptember-17	199.78	24	48.75	62.43	24	121.88	0	0	0	0	0	
tober-17	103.07		58.50	50.09							0	
	103.07 il 68805.63	12 7774	58.50 37898.25	50.09 10206.67	24 3207	117.00 15634.13	0 7395	0 57	0 11182	0 6	0 64465	

 Notes:
 Interface
 Interface
 Interface

 (a)
 Inert C&D materials (public fill) include bricks, concrete, building debris, rubble and excavated soil.

(b) Non-inert C&D materials include wastes such as general refuse and mixed construction waste.

(c) If necessary, use the conversion factor: 3/4 load of dumping truck being equivalent to  $6.5 \text{ m}^3$  by volume.

Annex K

Environmental Complaint/ Enquiry, Environmental Summons and Prosecution Log

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
November 2011	0	0
December 2011	0	0
January 2012	0	0
February 2012	0	0
March 2012	4	0
April 2012	0	0
May 2012	0	0
June 2012	2	0
July 2012	1	0
August 2012	0	0
September 2012	0	0
October 2012	0	0
November 2012	2	0
December 2012	0	0
January 2013	0	0
February 2013	1	0
March 2013	1	0
April 2013	0	0

Annex K Cumulative Complaint and Summons/Prosecutions Log

ENVIRONMENTAL RESOURCES MANAGEMENT

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
May 2013	0	0
June 2013	0	0
July 2013	0	0
August 2013	0	0
September 2013	0	0
October 2013	0	0
November 2013	0	0
December 2013	0	0
January 2014	2	0
February 2014	1	0
March 2014	1	0
April 2014	1	0
May 2014	0	0
June 2014	0	0
July 2014	2	0
August 2014	3	0
September 2014	2	0
October 2014	1	0
November 2014	0	0

<b>Reporting Month</b>	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
December 2014	0	0
January 2015	0	0
February 2015	1	0
March 2015	1	0
April 2015	0	0
May 2015	1	0
June 2015	1	0
July 2015	1	0
August 2015	1	0
September 2015	0	0
October 2015	0	0
November 2015	0	0
December 2015	0	0
January 2016	0	0
February 2016	0	0
March 2016	1	0
April 2016	0	0
May 2016	0	0
June 2016	0	0

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
July 2016	0	0
August 2016	0	0
September 2016	1	0
October 2016	0	0
November 2016	0	0
December 2016	0	0
January 2017	0	0
February 2017	0	0
March 2017	0	0
April 2017	0	0
May 2017	0	0
June 2017	0	0
July 2017	0	0
August 2017	0	0
September 2017	0	0
October 2017	0	0
Overall Total	32	0

#### ENVIRONMENTAL RESOURCES MANAGEMENT





賽馬會文物保育有限公司 The Jockey Club CPS Limited

# **ATKINS**

### Central Police Station Conservation and Revitalisation Project



### **INVESTIGATION REPORT**

#### **Basic Information of Enquiry**

Log Number:	2017/07/001
Date of Enquiry Received	31 July 2017 and 5 August 2017
Location	Project Site
Nature of Enquiry	Landscape and visual
Enquiry from	Ming Pao Newspaper

#### Details of Enquiry


Ming Pao, a Chinese newspaper in Hong Kong, has published two articles on 31 July 2017 and 5 August 2017, respectively, concerning the health condition of the retained trees *Aleurites moluccana* (Tree 6 and Tree 7) located at the prison yard of the CPS Site. The 31 July 2017 article indicated that pests were found on Tree 6 and 7 and the current amount of leaves on Tree 6 and Tree 7 have seemingly reduced in comparison with the photo of the trees which was said to be taken in December 2015, suggesting that the health of Tree 6 and Tree 7 may have deteriorated. The report enquired if the construction work has been carried out in compliance with the requirements in the Environmental Permit and potential measures to rectify the condition of Tree 6 and Tree 7. The 5 August 2017 article reported that the contractor has applied pesticides to the trees but queried if the contractor did not rectify the problem in a timely manner.

#### Investigation Report

- 1. Regular tree inspections have been carried out by a qualified arborist on a monthly basis in accordance with the requirement in the Environmental Permit (EP). The arborist will observe and identify any potential issues to the retained trees and recommend appropriate remedial actions as necessary. Routine horticultural operation for the retained trees has been undertaken, including watering of the trees for at least 2-3 times a week and adding mulch to the trees when necessary as recommended by the arborist. The latest tree inspection has been conducted by the arborist on 10 July 2017 and the observations and recommendations were reported in the Monthly Tree Inspection Report for July 2017 prepared by the arborist.
- 2. As indicated in the Monthly Tree Inspection Report for July 2017, signs of pests (*Trialeurodes vaporariorum*) have been observed on some faded leaves of Tree 6 and Tree 7 during the tree inspection on 10 July 2017. A decayed log was also found on the upper branches of Tree 7. The arborist has recommended the application of pesticides to Tree 6 and Tree 7 and pruning of the decayed log on Tree 7 to be conducted as soon as possible to control and eliminate the pests. Although there are signs of pests, the health condition of the trunks of Tree 6 and Tree 7 is considered fair by the arborist. Some young and green leaves are growing on Tree 6, but leaves on the crown of Tree 7 are observed to be rather sparse. The tree protection zone around the planters of Tree 6 and Tree 7 are also in good condition and the areas in the vicinity of the trees are clean and tidy.
- 3. After the tree inspection on 10 July 2017, application of pesticides on the tree crown of Tree 6 and Tree 7 and pruning of decayed log on Tree 7 have been arranged and conducted on 3 and 4 August 2017. Residents near the Project Site have been informed of the pesticide application dates in advance. Application of pesticides could not be arranged in July due to presence of frequent rainy days towards the end of July. A Registered Consulting Arborist assessed Tree 6 and Tree 7 on 12 August 2017. He commented that the pests on Tree 6 and Tree 7 appeared to be under control due to the pesticide application on 3 and 4 August 2017. According to the Registered Consulting Arborist, new and healthy branches and roots were observed on the trees. He advised the Contractor to maintain sufficient mulch in the planters and conduct regular watering to the trees. Further application of pesticides is considered not necessary at the moment but the arborist will continue to closely monitor the effectiveness of the pesticide and the health of the trees and apply further measures if required.
- 4. Tree 6 and Tree 7 were cordoned off with a fence of about 2.5m height as a tree protection zone since the commencement of the construction works on site in accordance with the requirement in Appendix Part B of the EP. The fence was removed in April 2016 due to various works at Prison Yard, including laying of floor paving, making of chairs next to the planters and planter repairing works, etc. Construction works have substantially completed at the Prison Yard but barricades are still being set up around Tree 6 and Tree 7 to cordon off the trees. No root pruning has been conducted for Tree 6 and Tree 7. A foliage sprinkler cleansing system was installed at Tree 6 and Tree 7 for washing off any accumulated dust from the leaves in accordance with the requirement in Appendix Part B of the EP. As no major construction works have been conducted at the Prison Yard since April 2016 and construction works have substantially completed since April 2017, accumulation of dust on the leaves is no longer expected and the foliage sprinkler cleansing system was removed since May 2017. The areas in the vicinity of Tree 6 and Tree 7 have generally been kept clean and tidy. Construction activities in the vicinity of Tree 6 and Tree 7 were kept at a minimum. Other mitigation measures for landscape and visual impacts as required under the EP are complied with. A wide tree strip for compensatory tree planting has been reserved at the eastern part of the Parade Ground in accordance with the requirement in EP Condition 2.9. Planters for the compensatory trees are currently being built.
- 5. Photo records of Tree 6 and Tree 7 taken during the monthly tree inspections from December 2015 to July 2017 were provided below for reference. It can be seen that there is a gradual loss of leaves at Tree 6 and Tree 7 since around May 2016. However, as it is considered there is still reasonable amount of leaves on Tree 6 and Tree 7 with no apparent issues on the health of the trees observed, no actions were recommended or taken by the arborist until pests were observed during the tree inspection on 10 July 2017. The arborist has suggested two possible reasons for the loss of leaves on Tree 6 and Tree 7 since around May 2016:

i) Presence of pests – Besides the pests (*Trialeurodes vaporariorum*) which were recently discovered during the tree inspection on 10 July 2017, Tree 6 and Tree 7 have also been infected with the pest Mealy Bugs in April 2016. Pests present on the leaves take up nutrients from the trees, causing loss of leaves and potential deterioration of the health of the trees. Subsequent application of pesticides and pruning of affected leaves and branches were performed on 25 April 2016 and proved effective with signs of pests apparently reduced and hardly found after the application. Although the trees were clear of pests after the pest application on 25 April 2016, gradual loss of leaves at Tree 6 and Tree 7 can be observed since around May 2016.

ii) Age of the trees – Tree 6 and Tree 7 were planted in 1960s and are currently about 50-60 years of age. According to the arborist responsible for the trees on site and other experienced arborists in Hong Kong, Aleurites moluccana (Tree 6 and Tree 7), which is a non-native species, generally has a life expectancy of about 60 to 80 years. The loss of leaves and possible deterioration of health may reflect the natural aging of the tree.

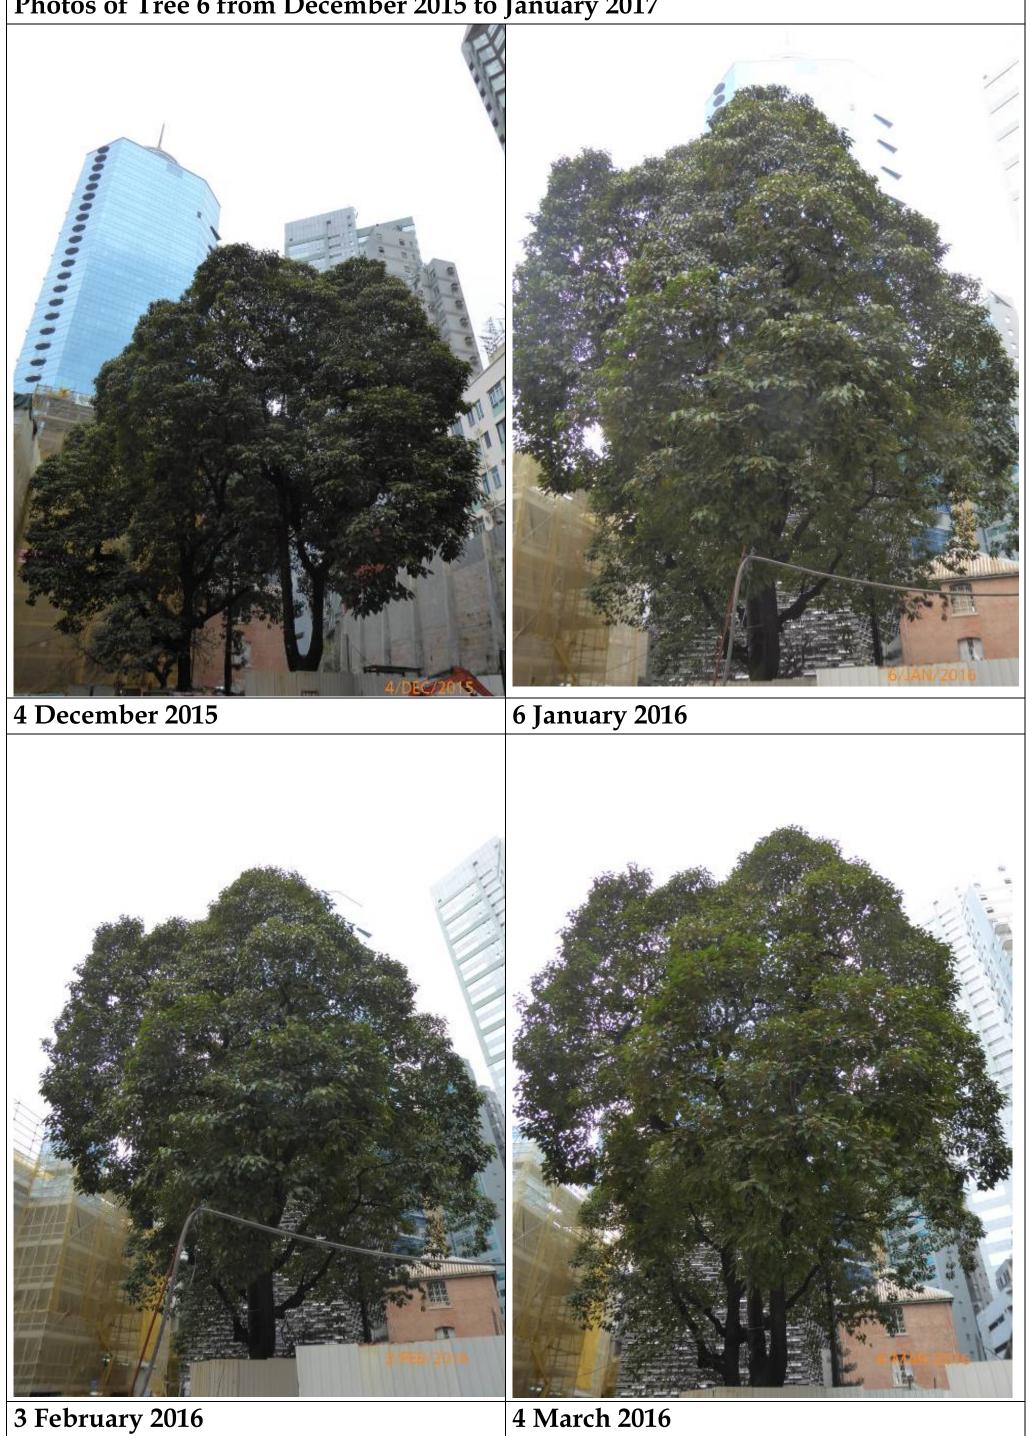




6 April 2016

4 May 2016




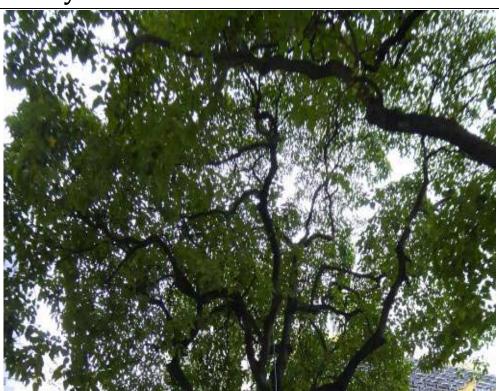


8 June 2016	4 July 2016





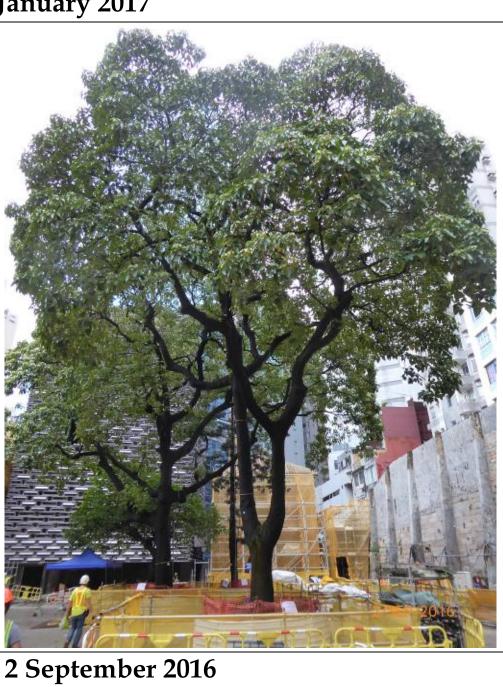

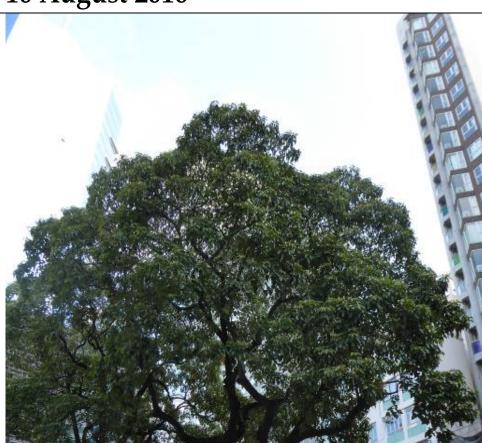




4 October 2016	2 November 2016









8 February 2017	15 March 2017

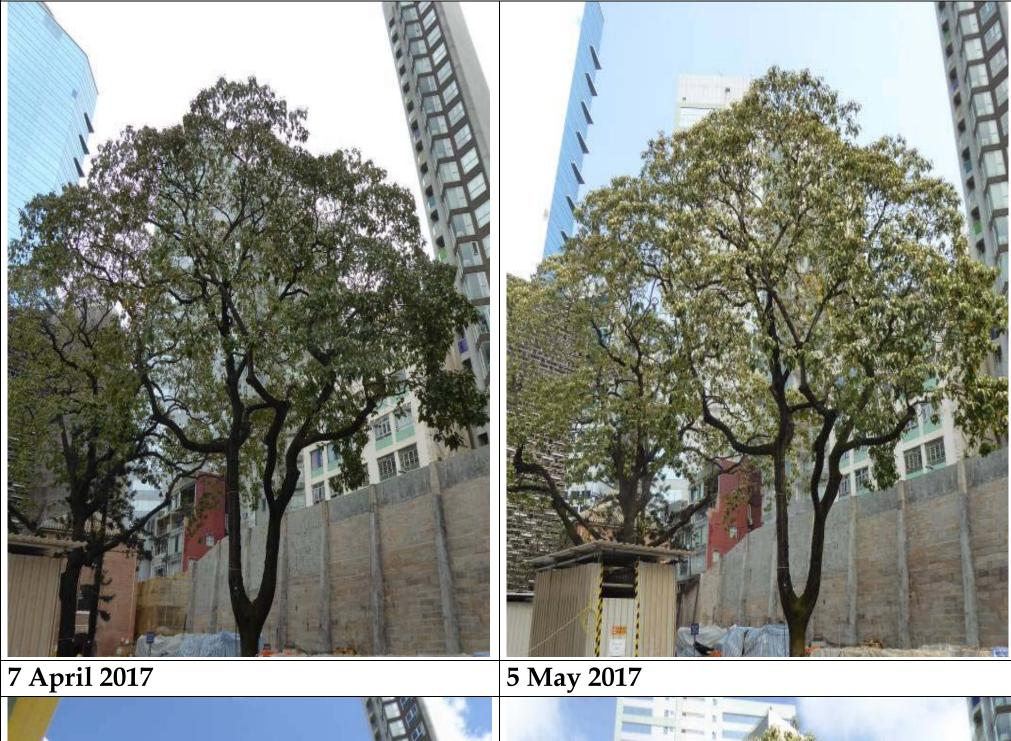






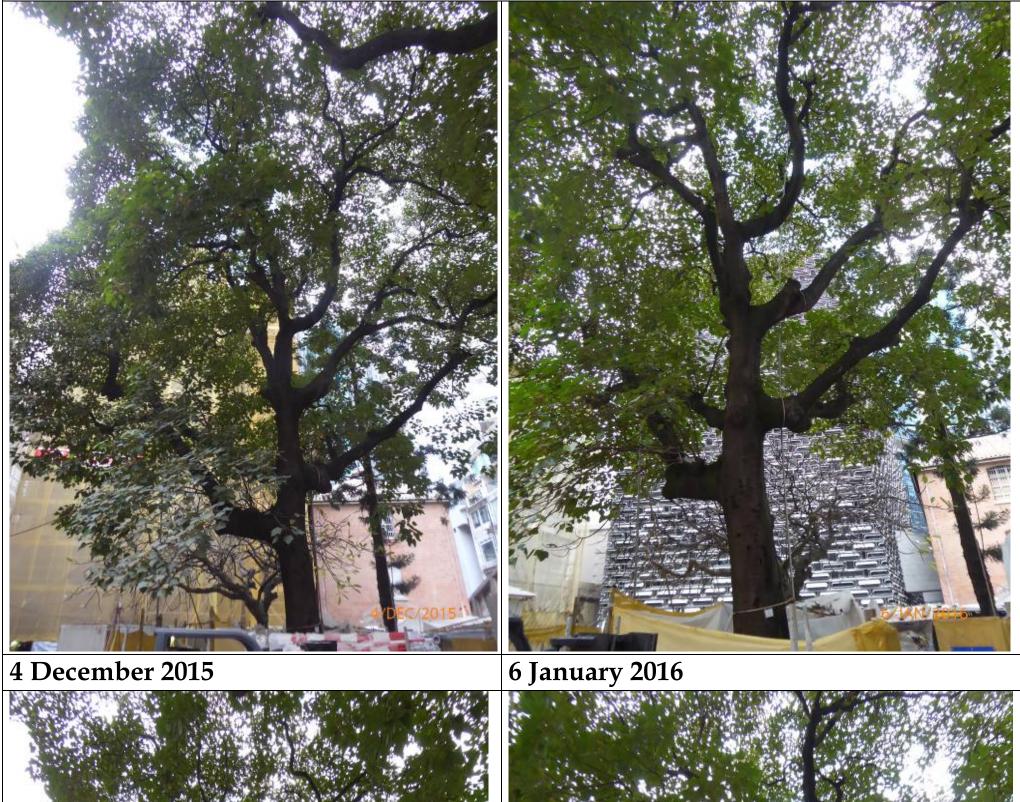





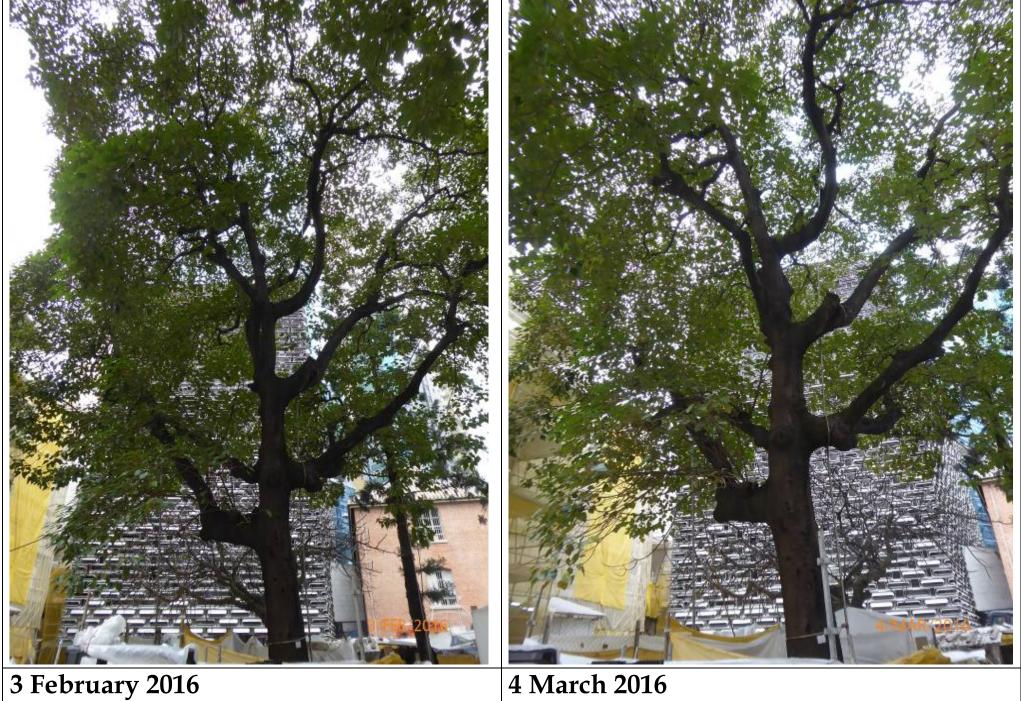







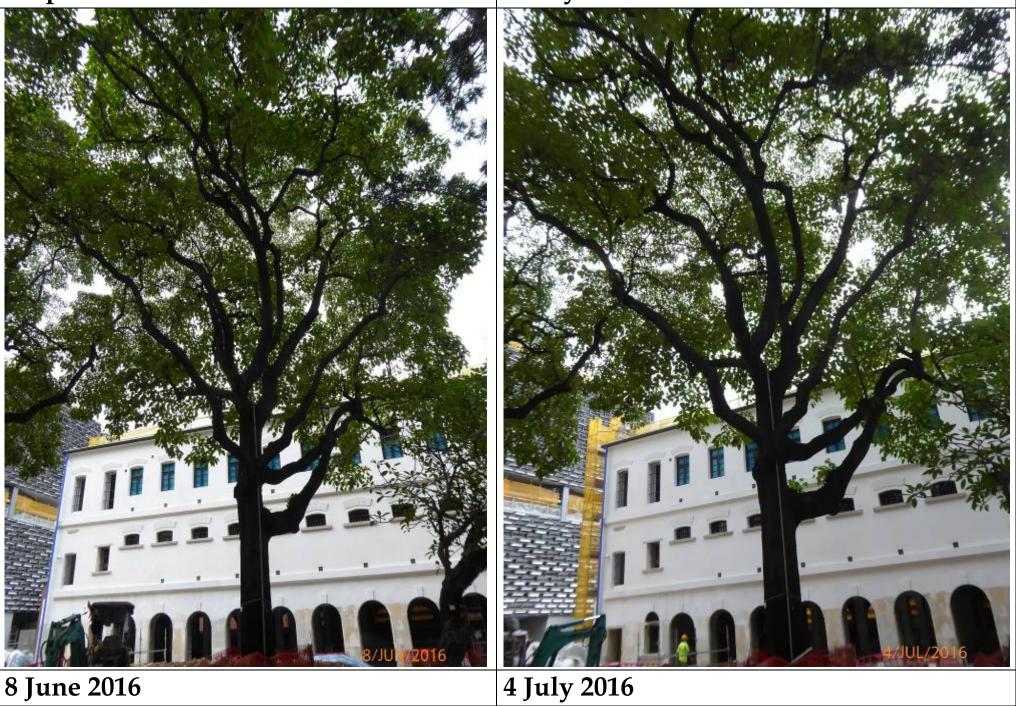

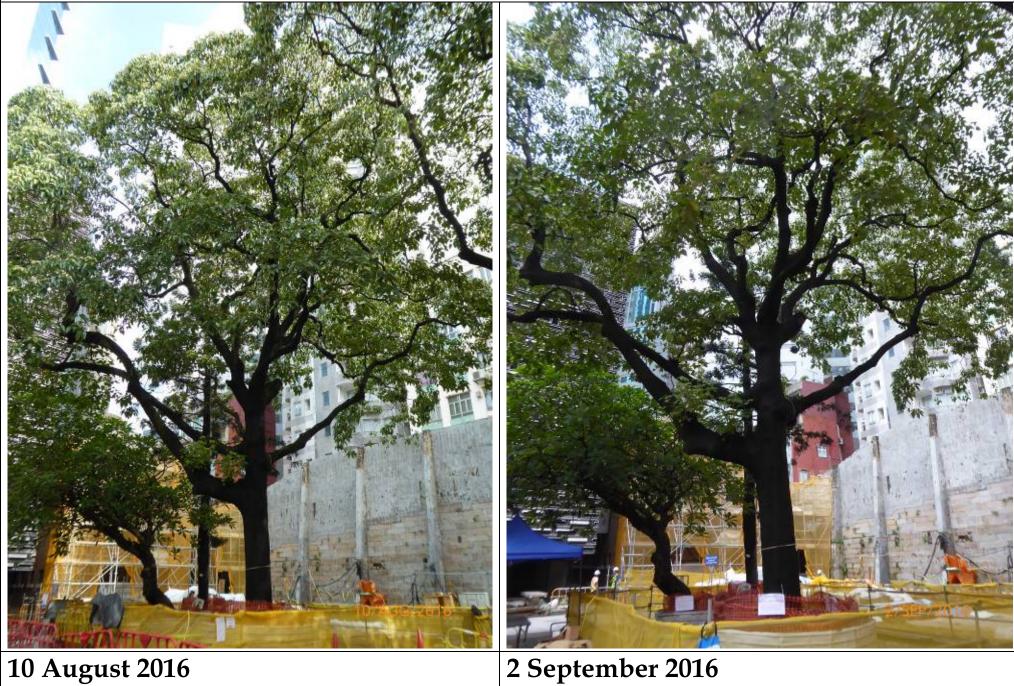


10 August 2016

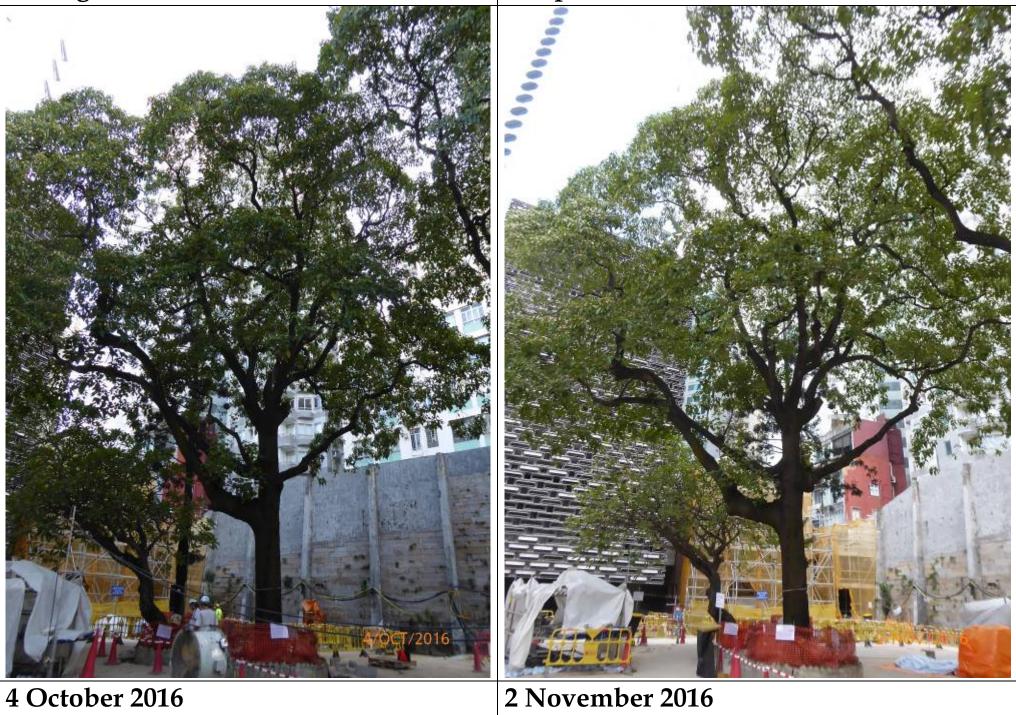

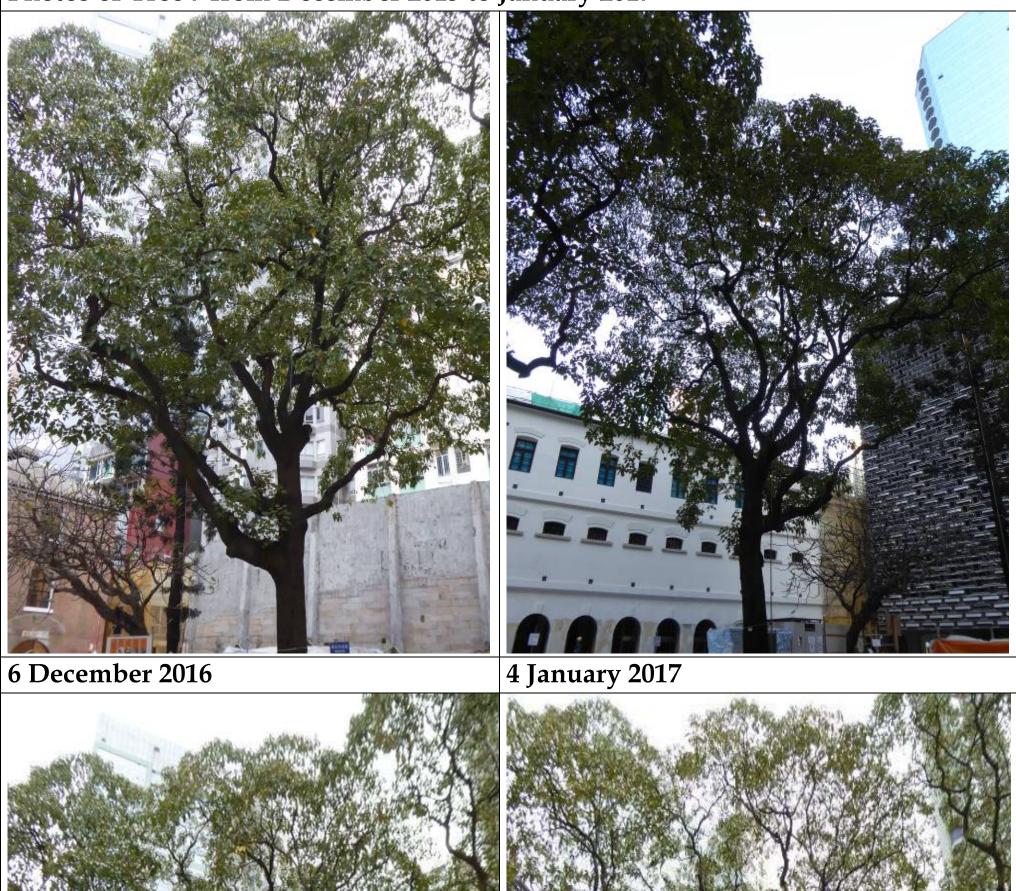






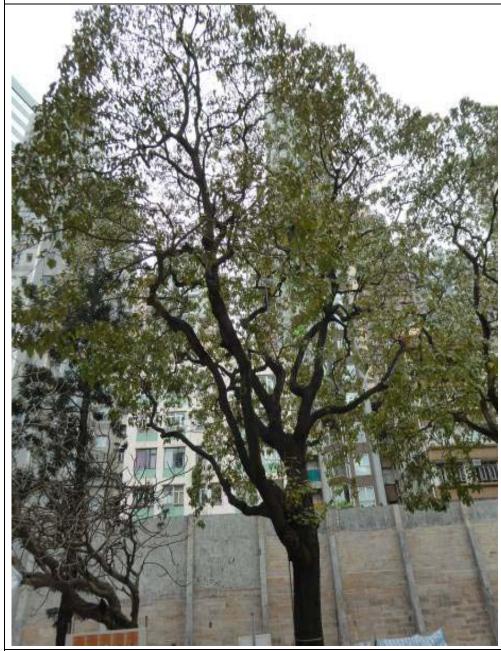




7 April 2017

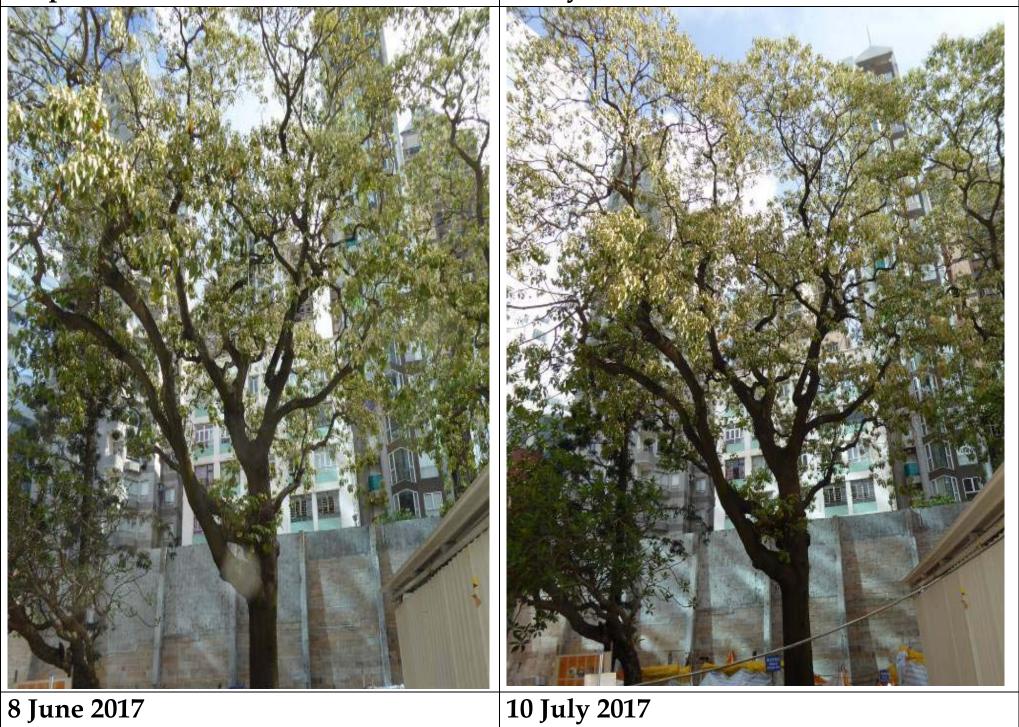

5 May 2017

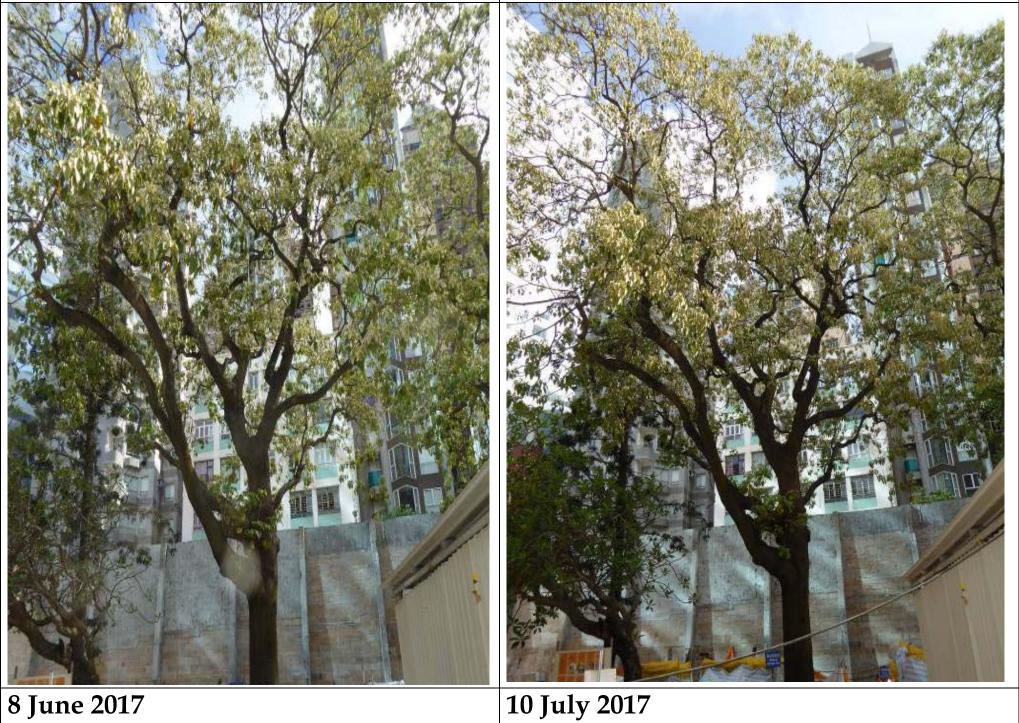

#### Mitigation Measures and Follow-up Actions Recommended to Contractor

All construction works are carried out strictly following the necessary requirements specified in the EP, EIA, and the EM&A Manual of this Project. Application of pesticides and pruning of decayed log have been conducted on Tree 6 and Tree 7 on 3 and 4 August 2017 after the discovery of the presence of pest (*Trialeurodes vaporariorum*) during the tree inspection on 10 July 2017. As observed by the arborist in the inspection on 12 August 2017, the pests on Tree 6 and Tree 7 appeared to be under control. Further application of pesticides is considered not necessary at the moment but the arborist will continue to closely monitor the effectiveness of the pesticide and the health of the trees and apply further measures if required.

In addition, HKJC is currently seeking another tree specialist to thoroughly assess the health conditions of Tree 6 and Tree 7 and will propose further special care and treatment measures on Tree 6 and Tree 7.

Date of File Closed : 25 August 2017

Approved by:

ET Leader

IEC

ICCPS's Representative

Rocco Design Architect's Representative

.

(Name: Katie Yu) Date: 25 August 2017

Gammon's Representative



(Name: Cliff Leung Date: 25 August 2017

(Name: Keith Chau) Date: 25 August 2017

(Name: KENNETH LEF Date: JS Ang 2017

(Name: KUNG Date: 75 Ary 2017

14

Annex L

Records of Vibration Monitoring for Other Construction Works

Structural Additions and



1 z	lock しし B.D. Rel No 用字目的事故版
15700 M	22-3/3066/10/BLK11 (HU) (S) F.S.D. Ref No 法防废搜索编数
BIE	Revisian/Submission 性改成/极批
	No.编述 Description 說明 Date 日期 Approved畫
the second	- BD SUBMISSION (50) 12/11 JS A BD SUBMISSION (01) 03/12 JS
44	B BC SUBMISSION (17) 03/12 JS C BD SUBMISSION RW BATCH 1 03/12 JS
Shiu King	D FOP INFROMATION (50) 03/12 JS E BD SUBMISSION (51) 05/12 JS
Cont	F BD SUBMISSION (04) 05/12 JS
1	H BD SUBMISSION (14) 05/12 JS
8. A. T	J BD SUBMISSION RW BATCH 7 06/12 JS K BD SUBMISSION (06&07) 07/12 JS
	L BD SUBMISSION (01)(H0)07/12 JS M BD SUBMISSION (11) 07/12 JS
and the second s	
25 - 42 C	
S & S A MAN	
1. 1. 1. 1. 1. 1. 1. 1. 1. 1. 1. 1. 1. 1	
provide a serie de la companya de la companya de la companya de la companya de la companya de la companya de la	Plan Approved
	CHIONG Kam-yuene Jacky
2.	Chief Structural Engineer for BUILDING AUTHORITY
all	- 3 OCT 2012
Cert.	
B/R176	Key Plan 索引圖
C. L . C 3	• • •
Ę	0 0
iipa <sub>c</sub>	• • • ///
	0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0
1. 1	0 0
UR/	e l
EN .	
T	BD SUBMISSION
M. E.	Drawing Status 裂麗狀況 This drawing and the contents berein are the copyright
CEOR FISHINGE MICE PHILE C	of relevant consultants. 本確認及其內容的版標屬有關觀問公司所非。 - No part of the drawing and the design contained herein
A S	may be reproduced without the pror written consent of relevant consultants. 未維有時期間公司書面印度。不否依對此服紙內任何
	内容或设计 - Do not take measurements directly from this crawing.
EXISTING FRESH WATER MAIN	切勿直兆從醫紙上豐度尺寸。 Check and vorify all dimensions on site 研有尺寸必须在工地現場抱意及審核。
	<ul> <li>Read this drawing in conjunction with the specifications and all other related drawings, 此關係必須與規格投明實及其它有關團級一併間講。</li> </ul>
STREET LIGHTING NC. 33488-A1	<ul> <li>Notify the relevant consultants immediately of any discrepancy found literein, 如發現內容有任何謬蹤之處。應立刻通知有質觀問公司。</li> </ul>
EXISTING STREET LIGHTING CABLE	如發現內容有任何謬欲之處。應立刻通知有質範間公司。 Client 聚主
EXISTING GAS MAIN	· 赛馬台文物保存有限公司
EXISTING HV ELECTRICITY CABLE	The Jecker Club CP Limited
EXISTING LV ELECTRICITY CABLE	
EXISTING TELECOMMUNICATION DUCT	
LIMITED)	
	Executive Architect / AP
	ROCCO 计字严
	Structural Engineer / RSE E & M Engineer
	ARUP RIJRP
	Project 項目 CENTRAL POLICE STATION
KISTING DRILLHOLE WITH TANDPIPE/PIEZONETER	CONSERVATION AND REVITALISATION PROJECT
ROPOSED BUILDING SETTLEMENT	Drawing Tate 蜀名 MONITORING LAYOUT PLAN
DINTS/TILTMETER	MONTONING LATOUT PLAN
ROPOSED RETAINING WALL SETTLEMENT DINTS/TILTMETER	
DINTS/TILTWETER ROPOSED INCLINOMETER TO BE BUILT IN	Scale 분명 Drawn 변문 Checked 문편
oints/tiltmeter Roposed inclinometer to be Built in Ored Pile Wall or Pipe Pile Wall	1:3009AI K.C.Loi AL Drawing No.圆型 Revision修改版
OINTS/TILTMETER ROPOSED INCLINOMETER TO BE BUILT IN ORED PILE WALL OR PIPE PILE WALL ROPOSED GROUND SETTLEMENT POINTS	1:3009AI K.C.Lai AL
oints/tiltmeter Roposed inclinometer to be Built in Ored Pile Wall or Pipe Pile Wall	1:3009AI K.C.Loi AL Drawing No.圆型 Revision修改版
OINTS/TILTMETER ROPOSED INCLINOMETER TO BE BUILT IN ORED PILE WALL OR PIPE PILE WALL ROPOSED GROUND SETTLEMENT POINTS	1:3009AI K.C.Lai AL Drawing No.圆型 Revision增改图
	BURITAS EXISTING FRESH WATER MAIN EXISTING FOLL COMUNICATION DUCT (MITTING TELECOMUNICATION

# Vibration Monitoring Record (August 2017)

	Block 11	
Point	VM11-1	VM11-2
Date	mm/s	mm/s
01-Aug-17	0.105	0.109
02-Aug-17	0.109	0.104
03-Aug-17	0.128	0.105
04-Aug-17	0.125	0.108
05-Aug-17	0.107	0.102
06-Aug-17	Sun	iday
07-Aug-17	0.113	0.105
08-Aug-17	0.117	0.108
09-Aug-17	0.105	0.104
10-Aug-17	0.111	0.107
11-Aug-17	0.118	0.102
12-Aug-17	0.102	0.107
13-Aug-17	Sun	iday
14-Aug-17	0.109	0.104
15-Aug-17	0.107	0.106
16-Aug-17	0.114	0.101
17-Aug-17	0.111	0.112
18-Aug-17	0.101	0.109
19-Aug-17	0.105	0.102
20-Aug-17	Sun	iday
21-Aug-17	0.104	0.107
22-Aug-17	0.109	0.102
23-Aug-17	Typhoon	
24-Aug-17	0.103	0.107
25-Aug-17	0.109	0.110
26-Aug-17	0.115	0.102
27-Aug-17	Sun	iday
28-Aug-17	0.104	0.106
28-Aug-17 29-Aug-17	0.104 0.105	0.106 0.102

# Vibration Monitoring Record (September)

	Block 11	
Point	VM11-1	VM11-2
Date	mm/s	mm/s
01-Sep-17	0.105	0.102
02-Sep-17	0.109	0.106
03-Sep-17	Su	nday
04-Sep-17	0.127	0.102
05-Sep-17	0.105	0.106
06-Sep-17	0.110	0.103
07-Sep-17	0.107	0.102
08-Sep-17	0.102	0.105
09-Sep-17	0.105	0.103
10-Sep-17	Su	nday
11-Sep-17	0.109	0.104
12-Sep-17	0.105	0.102
13-Sep-17	0.111	0.106
14-Sep-17	0.125	0.109
15-Sep-17	0.106	0.102
16-Sep-17	0.106	0.105
17-Sep-17	Su	nday
18-Sep-17	0.114	0.109
19-Sep-17	0.109	0.102
20-Sep-17	0.102	0.106
21-Sep-17	0.109	0.105
22-Sep-17	0.117	0.109
23-Sep-17	0.112	0.111
24-Sep-17	Sunday	
25-Sep-17	0.108	0.102
26-Sep-17	0.105	0.105
27-Sep-17	0.119	0.107
28-Sep-17	0.107	0.105
29-Sep-17	0.109	0.115
30-Sep-17	0.109	0.109

# Vibration Monitoring Record (October)

	Block 11		
Point	VM11-1	VM11-2	
Date	mm/s	mm/s	
01-Oct-17	Su	nday	
02-Oct-17	The day followi	ng National Day	
03-Oct-17	0.110	0.101	
04-Oct-17	0.104	0.106	
05-Oct-17	The day following the Fes	Chinese Mid-Autumn stival	
06-Oct-17	0.113	0.107	
07-Oct-17	0.113	0.107	
08-Oct-17	Su	nday	
09-Oct-17	0.109	0.104	
10-Oct-17	0.105	0.109	
11-Oct-17	0.107	0.104	
12-Oct-17	0.109	0.103	
13-Oct-17	0.118	0.103	
14-Oct-17	0.104	0.101	
15-Oct-17	Sunday		
16-Oct-17	0.112	0.104	
17-Oct-17	0.105	0.102	
18-Oct-17	0.109	0.109	
19-Oct-17	0.115	0.103	
20-Oct-17	0.109	0.105	
21-Oct-17	0.115	0.103	
22-Oct-17	Sunday		
23-Oct-17	0.107	0.106	
24-Oct-17	0.110	0.109	
25-Oct-17	0.116	0.104	
26-Oct-17	0.109	0.102	
27-Oct-17	0.126	0.106	
28-Oct-17	Chung Yeu	ung Festival	
29-Oct-17		Sunday	
30-Oct-17	0.109	0.103	
31-Oct-17	0.114	0.104	

Annex M

Summary of Condition of Character Defining Elements, Historic Buildings and Structures

**CENTRAL POLICE STATION, HONG KONG** 

#### SCHEDULE OF CHARACTER DEFINING ELEMENTS

This Schedule of Character Defining Elements has been prepared at the request of the Antiquities and Monuments Office (AMO) to support applications for S.6 approval under the Antiquities and Monuments Ordinance and the Environmental Impact assessment Ordinance. The levels of significance and their meanings are derived from the work of James Semple Kerr.

For each element, the level of significance is stated, together with the planned outcome and associated mitigation measure, where applicable, and the resultant impact upon the significance. Generally, only those items subject to change are noted, and the impacts should be read as negative. Where elements are deemed currently to be adverse, the impact of the changes should be read as positive.

The levels of significance and definitions as defined by Kerr are stated below. The criteria used to assess the significance of each element are, as directed by AMO : (i) the association with the operation of the Central Police Station Compound; and (ii) its architectural quality. Where these criteria conflict, the resultant assessment score is aggregated.

Each entry in the schedule is accompanied by a photograph of a sample of the item described. The location of each photograph is noted on the floor plans attached in the appendix to the schedule. Similar examples of each item can be seen by observation.

# **Central Police Station**

	Level of significance	Meaning			
	Exceptional	Where an individual space or element is assessed as displaying a strong contribution to the overall significance of the place. Spaces, elements or fabric exhibit a high degree of intactness and quality, though minor alterations or degradation may be evident.			
Positive	High	Where an individual space or element is assessed as making a substantial contribution to the overall significance of the place. Spaces, elements or fabric originally of substantial quality, yet may have undergone considerable alteration or adaption resulting in presentation which is either incomplete or ambiguous. The category also includes spaces, elements or fabric of average quality in terms of design and materials, but which exhibit a high degree of intactness.			
	Moderate	Where an individual space or element is assessed as making a moderate contribution to the overall significance of the place. Spaces, elements or fabric originally of some intrinsic quality, and may have undergone alteration or degradation. In addition, elements of relatively new construction, where the assessment of significance is difficult, may be included. This category also includes original spaces, elements or fabric of any quality which have undergone extensive alteration or adaption.			
	Low	Where an individual space or element is assessed as making a minor contribution to the overall significance of the place, especially when compared to other features. Spaces, elements or fabric originally of little intrinsic quality, any may have undergone alteration or degradation. This category also includes original spaces, elements or fabric of any quality which have undergone extensive alteration or adaption to the extent that only isolated remnants survive (resulting in a low degree of intactness and quality of presentation).			
	Neutral	Where an individual space or element is assessed as having an unimportant relationship with the overall significance of the place. Spaces, elements or fabric are assessed as having little or no significance.			
	Adverse	Where an individual space or element detracts from the appreciation of cultural significance, by adversely affecting or obscuring other significant areas, elements or items.			

# **Central Police Station**

Addendum	Date
Item no. 10.029 edited entry	18 June 2013
Item no. 10.030 added	18 June 2013

### **Central Police Station**

#### **01** Police Headquarters

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.001	Flat plywood ceiling lining with plain rectangular cover battens		Adverse	Replace with T&G boarding to match existing	Not applicable	High
01.002	Plaster coving at abutments of walls and ceilings		Low	Remove in exceptional cases eg, where adjacent new lift shaft	Cut back neatly to a square edge and ensure remaining section is secure.	Low

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.003	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
01.004	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.005	Plaster box cornice		Moderate	Remove in exceptional cases eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate
01.006	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re- used.	Moderate

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.007	External shutters		High	Reinstate to match existing pattern	Not applicable	High
01.008	External terraces at 1/F		High	Overlay existing concrete paving with timber deck to provide level access	New deck to be reversible	Low

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.009	Plaster ceilings on GF and LG1		Moderate	Install cloud ceilings to accommodate new services	Install fixed grid to minimise damage to ceiling	High
01.010	Timber door frames and architraves		Moderate	Conceal in exceptional cases eg. where adjacent new lift shaft	Retain architrave and door frame in situ. Avoid damage to joinery.	High

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.011	Concrete floor		Low	Replace where new kitchens and plant rooms to be installed	Carefully remove and retain existing floorboards for re-use. Ensure controlled demolition of concrete structure and removal of debris from building to avoid damage to adjacent surfaces. Protect or carefully remove and set aside adjacent elements such as skirting boards	Low

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.012	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.014	Existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non- combustible sheet linings to block opening.	Moderate
01.015	Existing walls		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.016	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
01.017	Mezzanine floor in room 01/LG1/13		Adverse	Remove floor and supporting columns to re-create original double-height space	Not applicable	High

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.018	Cast iron grilles above Service Corridor 01/LG1/35		High	Remove existing steel sheet covering [alterations to grilles awaiting confirmation from HdM]		
01.019	Perforated concrete deck above lightwell		Adverse	Remove deck and make good brickwork at abutments	Not applicable	High

November 2012 Draft 10
Purcell Miller Tritton LLP

### **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.020	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
01.021	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non- compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

# **Central Police Station**

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.022	Main corridors		High	Install new lighting, fire sprinklers, fire doors to comply with Fire Services Code	New fittings to be mounted in a manner that is of its time and reversible. Avoid physical intervention with existing plaster box cornices, architraves, dado rails	High
01.023	Painted signs	LOCKLEFT	High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.024	Fixed signs		Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.025	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material in a neutral mid-tone.	High

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.026	Enclosure at First Floor landing of main stair		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.027	Steel railing enclosure at FF level		Low	Remove	Record on measured drawings and photographs	Low
01.028	Tongued and grooved flat and sloped timber boarded ceilings		Moderate	Repair where necessary and reinstate where missing	Not applicable	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.029	Modern partitions		Adverse	Remove	Not applicable	High
01.030	Tiled dado		High	Cut away for enlargement of existing windows to form new doorways	Cut back to joint line and adjust tiling pattern to suit new opening. New tiles to match existing sizes and colours.	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.031	Reinforced concrete canopy and sash windows		Moderate	Remove canopy and replace sash windows with new windows to match original	Make good brickwork where canopy removed, Reinstate rendered architraves around new window to match similar window facing on West wing	Moderate

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.032	Arched opening in brick wall above ceiling line		Low	Retain insitu and use to pass through future services. Infill only where opening is within a fire compartment	Use non-combustible material to block opening.	Low

Element no.	Description	Photo ref	Significance	Proposal	Mitigation	Impact
01.033	Ceiling void service installation (Cast Iron Water Tank and pipework)		Low	Remove and make good adjacent surfaces	N/A	Low

### **Central Police Station**

#### 02 Armoury

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
02.002	Modern internal doors		Adverse	Remove	Not applicable	High

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.003	Modern partitions		Adverse	Remove	Not applicable	High
02.004	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.005	Brickwork walls enclosing rooms at GF and FF East side		Low	Remove and reinstate verandah	Not applicable	High
02.006	Concrete floors		Low	Selected removal to accommodate new stairs and lift shaft	Carefully form openings to ensure structural stability	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.007	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.008	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.009	Concrete stairs		Adverse	Remove stairs	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
02.010	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts to reduce impact. Finish ducts in a non- reflective material that is neutral in colour and mid-tone.	High
02.011	Roof structure and tiled soffit		High	Repair and retain.	N/A	Neutral

#### 03 Barracks Block

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
3.002	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where item cannot be re-used.	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.003	External shutters		High	Reinstate to match existing pattern	Not applicable	High
03.004	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.005	Timber spandrel panels below windows		Low	Conceal in exceptional cases eg. where adjacent new lift shaft	Retain frame and spandrel panel where possible. Remove only where necessary in connection with re- planning of interiors. Record on measured survey drawings.	Low
03.006	Timber floors		High	Replace where new kitchens and plant rooms to be installed	Limit extent of removal as much as possible. Carefully remove and retain existing floorboards for re-use. Ensure controlled dismantling of timber structure and set aside for possible re-use. Protect or carefully remove and set aside adjacent elements such as skirting boards	Medium

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.007	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.008	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
03.009	Block existing door openings		Low	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non- combustible sheet linings to block opening.	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.010	Form new door openings		Low	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance. Re-open original openings where possible. Retain original reveals and arches.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.011	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.012	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
03.013	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non- compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.014	Painted signs	NO VISITOR WILL BE ADMITTED WITHOUT THE PERMISSION OF THE D.O. OR FORMATION COMMANDER 或官管主得未如者訪探 進撞得不可許官警值當	High	Protect in situ	Not applicable	N/A
03.015	Fixed signs	NO. 3 PLATOON R. & F CHANGING ROOM 第三隊更衣室	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.016	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
03.017	Lean-to structure adjacent North wall		Moderate	Remove	Record on measured survey drawings. Make good walls where roof structure abuts	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.018	Metal-frames windows at GF North elevation		Adverse	Remove window frames, masonry spandrel panels below and reinstate verandah	Not applicable	High
03.019	Internal walls at Ground Floor level		Moderate	Remove selected internal walls where strictly necessary as part of re- planning of interiors	Walls of early or original date to be retained in part eg. by leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not re- bonded. Record walls on measured survey dwgs.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.020	Assembly rooms at centre of building (all floors)		Moderate	Sub-divide two rooms on each floor to provide service core, comprising: lifts, toilets, plant rooms, stores	Form new sub-visions using lightweight partitions to achieve reversibility. Form straight joints at abutments with existing retained walls. Notch new partitions around existing brick corbels at high level as a reminder of current condition.	Moderate
03.021	Exposed soffits of timber floors		Moderate	Underline existing floors to achieve specified fire resistance stated in Code	Avoid unnecessary damage to existing structure. New lining will reduce extent of intervention into existing structure. Keep level of new linings well clear of window heads.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.022	Existing window frames/openings		High	Open up selected openings to form new fire escape doors	Retain any salvageable material for possible re- use elsewhere. Retain existing window jambs intact. Cut away masonry to form door openings along same line as window jamb; do not re-bind cut brickwork. Record existing condition on measured survey drawings.	Low
03.023	Single storey outbuildings on south side		Adverse	Demolish	Check for evidence of early route from Magistracy to Prison.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.024	Bridge at east end		Moderate	Retain	Not applicable	Neutral

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.025	Chimneypiece on Ground Floor		Low	Repair and retain in current location	Not applicable	Neutral
03.026	Window in south wall; original dormitory space		Moderate	Remove window and take down brickwork spandrel; subdivide space to form new fire- protected escape route.	Record existing condition on measured survey drawings. New partition wall to be reversible.	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
03.027	Clay-tiled floor in store room adjacent stairs		Low	Remove as part of re- planning of interiors	Record on measured survey drawings	Low

### **Central Police Station**

#### 04 Dormitory Block A & B

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
04.002	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.003	Plaster box cornice		Moderate	Remove in exceptional cases where eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.004	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.005	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non- combustible sheet linings to block opening.	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.008	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.009	Window frames in arcades of North and East elevations		Adverse	Remove window frames and make good masonry reveals and reinstate verandah	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.010	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.011	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non- compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.012	Stair from First to Second Floor		High	Replace stair to improve safety	New stair to be built of steel to comply with Code and to distinguish it as being "of its time".	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.013	External verandahs		High	Install new lighting, fire sprinklers, fire doors to comply with Fire Services Code, extract ducting to external walls	New fittings to be mounted in a manner that is of its time and reversible. Avoid physical intervention with existing plaster box cornices in rooms, architraves, dado rails. Position outlet grilles in extneral walls on centre- line of arcade arches and above structural arch	High

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.014	Painted signs	BLOCK A	High	Protect in situ	Not applicable	N/A
04.015	Fixed signs		Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.016	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.017	Toilets at ends of verandahs		Adverse	Remove and make good finishes	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.018	Partitions at GF Dormitory A		High	Remove to make way for Interpretation	Prepare measured drawings and photographs before removal.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.019	Switchgear in old porch 04/G/13		Adverse	Open up porch, remove electrical switchgear and make good	Not applicable	High

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.020	Flat plywood ceiling lining with plain rectangular cover battens		Adverse	Replace with T&G boarding to match existing	Not applicable	High

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.021	Steps up to doorway on FF verandah		Moderate	Remove steps and doorway to form new fore escape route	Record steps and doorway on measured drawings	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.022	Timber boarded floors with moulded skirtings		High	Retain all boarded floors and skirtings	Reinstate floor boards and skirtings after fire proofing works	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.023	Cantilever balconies		High	Retain and repair as necessary. Reinstate balcony on west elevation.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.024	Clay tile floor		Low	Retain and repair as necessary	Not applicable	Neutral
04.025	Matched- boarded ceiling with perforated border		Moderate	Repair and retain insitu	Not applicable	Neutral

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
04.026	Ceiling rose		Low	Repair and retain insitu	Not applicable	Neutral

## **Central Police Station**

#### 06 Dormitory C

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.001	Granite thresholds at external doors		Low	Retain; install timber deck flush with level of step where necessary	Avoid alteration to step.	Low
06.002	Pitched roof		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.003	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High
06.004	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.005	Altered doors and windows		Adverse	Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable
06.006	External airconditioning units and other external services		Adverse	Adverse	Remove and make good brickwork	Not applicable

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.007	Painted signs	CECCECC	High	Protect in situ	Not applicable	N/A
06.008	Fixed signs	有生著 DEPARTMENT OF HEALH 中央 警署 診療所 POLICE MEDICAL POST CENTRAL POLICE STATIN	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.009	Cantilever balconies		High	Retain and repair as necessary.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low
06.010	Iron balustrades		High	Retain and repair as necessary.	Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.011	Perforated margin at perimeter of ceiling		Low	Repair and retain.	Where fire-proofing of floor is required, use a product that can be installed within the floor void, leaving the ceiling lining intact.	Low
06.012	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non- combustible sheet linings to block opening.	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.013	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate
06.014	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non- compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.015	Timber floors		High	Retain all boarded floors and skirtings	Reinstate floor boards and skirtings after fire proofing works	Low
06.016	Vinyl tile floor		Adverse	Remove tiles; renew boarded floor boards if necessary	Not applicable	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
06.017	Batten and panel ceiling lining		Low	Replace with lath and plaster ceiling	Not applicable	Low
06.018	Exposed roof covering		Moderate	Retain as existing	Consider insulating between upper and lower layers of roof tiles to provide thermal insulation and vapour barrier	Low

#### 07 Dormitory D

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.001	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
07.002	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
07.004	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.005	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
07.006	Clothes drying racks		Adverse	Remove	Not applicable	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.008	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
07.009	Corbelled brickwork at perimeter of room		Low	Remove in exceptional cases where eg. where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.010	Plywood floor		Adverse	Replace with hardwood floor boards	Not applicable	High
07.011	Timber thresholds at external doors and internal doors between main corridor and individual rooms		Low	Remove to enable level access	Splice extensions to door jambs, extend width of bottom rail of doors to match existing	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.012	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate
07.013	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non- compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.014	Fixed signs	中央子子会子会子 Control 1: tree Stanue Acellent Por 二日 社会社 月 王 日本 日本 日 王 日本 日本 日 日 日本 日本 日 日 日 日 日 日 日 日 日 日 日 日	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
07.015	Exposed roof tiling		Moderate	Retain as existing	Consider insulating between upper and lower layers of roof tiles to provide thermal insulation and vapour barrier	Low
07.016	Concrete floor		Adverse	Overlay with hardwood floor boards	Not applicable	Moderate

### **Central Police Station**

#### **08 Ablutions Block**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.001	Panelled doors		Low	Replace where necessary to achieve compliance with Building Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate
08.002	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	No applicable	High

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High
08.004	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non- combustible sheet linings to block opening.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.005	Timber roof structure		High	Retain	Not applicable	Neutral
08.006	External stair at west end		Moderate	Retain	Repair as necessary. Alter balustrade to achieve reasonable level of operational safety. Restrict access to repairs and maintenance and means of escape.	Low

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.007	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
08.008	Painted signs	NO VISITOR WILL BE ADMITTED WITHOUT THE PERMISSION OF THE D.O. OR FORMARIO/FORMANDER 支官查達羅本如者分辨 道證得來可非當查頂書	High	Protect in situ	Not applicable	N/A

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.009	Wire mesh screens		Adverse	Remove	Not applicable	Low
08.010	Internal walls and concrete floors		Low	Remove and rebuild in new configuration to suit new use	Ensure retained facades are fully supported during construction operations. Protect retained walls against damage during demolition works. Install new walls and floors to respect fenestration; avoid	Low

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
					clashes.	
08.011	Cantilever balconies on north side		Moderate	Repair and retain insitu	Not applicable	

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.012	Bridge access to Barrack Block		Moderate	Retain	Repair as necessary. Alter balustrade to achieve reasonable level of operational safety. Restrict access to repairs and maintenance and means of escape.	Low
08.013	Balcony balustrades		Low	Repair as necessary and retain. Remove selected sections to enable installation of new bridge connections to Barrack Block.	Avoid removal of associated iron columns. Form interventions at selected positions so as to maintain the rhythm of the balustrades and ensure proper support at ends.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
08.014	Single-storey outbuilding with pitched roof over		Low	Demolish to make way for new loading bay.	Record on measured survey drawings. Infill existing internal opening leaving reveals exposed. Tooth-in new brickwork at abutments after existing walls removed. Salvage cast iron columns for possible re-use.	Low
08.015	Corrugated steel sheet on balcony balustrades		Adverse	Remove	Not applicable	Low

**Central Police Station** 

### **Central Police Station**

#### 09 Magistracy

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
09.002	Modern partitions		Adverse	Remove	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.003	Internal walls		Moderate	Remove selected internal walls where strictly necessary as part of re- planning of interiors	Walls or early or original date to be retained in part eg. By leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not re- bonded, as evidence of the current condition.	Moderate
09.004	Plaster box cornice		Moderate	Remove in exceptional cases eg. Where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.005	Panelled doors		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non- combustible sheet linings to block opening.	Moderate
09.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.008	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non- compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate
09.009	Fixed signs		Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.010	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
09.011	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.012	Rainwater goods		Moderate	Replace with larger sizes/closer spacing to improve performance	Use cast iron to match original pattern Make good all redundant fixing holes	High
09.013	Metal walkways across lightwell		Adverse	Remove walkways and make good brickwork at abutments	Not applicable	High

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.014	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
09.015	Sloping canopy over external stair on west side		Adverse	Remove canopy and supporting structure	Not applicable	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.016	Single storey secure shelter at North West corner		Low	Demolish	Make good brickwork at abutments.	Low
09.017	Iron railing adjacent south side of item 09.016 above		Moderate	Retain; including remains of bars (now removed) between existing railings and east side of Barracks Block.	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.018	Public toilets in 09/LG1/17, 24		Adverse	Strip out sanitaryware, and fit-out for pottery display/service access. Form new door openings in east walls.	Retain existing door openings and metal- barred gates. Retain external granite steps and existing ground level.	Low
09.019	Cell doors		High	Re-open to provide access to Retail space	Retain existing iron gate	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.020	Meeting room at G/02-05		Moderate	Remove timber panelling from walls and sub divide to form new toilets and lift shaft	Record existing wall linings, and any earlier lining behind, on measured survey drawings.	Moderate
09.021	Lobbies within entrance hall G/12		Adverse	Remove	Not applicable	N/A

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.022	Public galleries on FF		Adverse	Strip out plant, remove partition walls and restore galleries	Not applicable	High
09.023	Chimney piece		Moderate	Retain	Not applicable	Neutral

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.024	Lanterns above entrance hall		Adverse	Remove existing lanterns and install single lantern	Not applicable	Moderate
09.025	Boarded ceilings on Second Floor		High	Repair and retain where possible	Limit extent of penetrations as far as practicable. Record on measured survey drawings where ceilings have exceptionally to be removed.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
09.026	Iron gates at top of external stair		Moderate	Retain	No applicable	Neutral
09.027	Iron balustrade adjacent terrace at First Floor east side		High	Retain; install structural glass balustrade inboard of ironwork to provide compliance with Building Codes	Avoid penetration of existing tiled pavement when fixing glass balustrade.	Low

### **Central Police Station**

#### **10** Assistant Superintendent's Office

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High
10.002	Plaster box cornice		Moderate	Remove in exceptional cases eg. Where adjacent new lift shafts	Cut back neatly to a square edge and ensure remaining section is secure.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.003	Panelled doors and linings		Moderate	Replace where necessary to achieve fire resistance to comply with Code	Re-use where possible. Record design on survey drawings where element cannot be re-used.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.004	Timber boarded floor with moulded skirtings		High	Repair as necessary and retain	Lift carefully and refix upon completion of fire- proofing and services installation	Low
10.005	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.006	Block existing door openings		Moderate	Block opening as part of re-planning of interior	Retain existing door frame and architraves. Use framing and non- combustible sheet linings to block opening.	Moderate
10.007	Form new door openings		Moderate	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.008	Altered doors and windows		Adverse	Repair or renew as necessary existing frames to match original patterns	Not applicable	High
10.009	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.010	Stair balustrades		High	Balustrades to be supplemented with additional handrails and supports to mitigate non- compliance with code	New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.011	Fixed signs		Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
10.012	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.013	Internal walls		Moderate	Remove selected internal walls where strictly necessary as part of re- planning of interiors	Walls or early or original date to be retained in part eg. By leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not re- bonded, as evidence of the current condition.	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.014	Partitions on SF		Moderate	Remove partitions	Record partitions on measured drawings	Moderate
10.015	Blocked windows on south elevation of south-east wing		Adverse	Re-open window openings and reinstate window frames and glazing	Not applicable	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.016	Open-joisted ceiling on Ground Floor of south- east wing		Moderate	Underline floor to provide fire protection.	Avoid intrusive alteration. Use fire-proofing products and methods that enable existing structure and boarding to be retained.	Low
10.017	Moulded timber picture rail		Low	Repair and retain	Not applicable	Neutral

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.018	Timber roof structure above south-east wing		Moderate	Repair as necessary and retain	Avoid intrusive alteration. Retain open appearance/	Low
10.019	Timber stair		Moderate	Underline with fire- resisting lining	Repair as necessary and retain.	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.020	Clay/terrazzo tile floor on Ground Floor and steps		Adverse	Adjust levels to enable level access and replace floor finish	Not applicable	Low
10.024	Granite wall on North elevation		High	Construct new external steps adjacent wall	Keep new stair clear of wall; avoid any physical connection between steps and wall.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.025	Single storey outbuilding at South East corner		Moderate	Demolish outbuilding and make good at abutments	Record outbuilding on measured drawings	Low
10.026	Blocked archway on East elevation		Adverse	Demolish infilling and re- open archway	Protect original arch and jambs against damage during demolition	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.027	Chimney on east elevation		Low	Retain	Not applicable	Neutral
10.028	Cantilever balconies		High	Repair as necessary and retain	Avoid intrusive interventions. Restrict access if necessary to retain existing appearance.	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
10.029	Steps on east elevation		Moderate	Repair as necessary and retain	Not applicable	Neutral
10.030	Decorative metal screen (See also item 10.026)		Low	Repair and retain	Not applicable	Positive

### **Central Police Station**

#### 11 A Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.001	Form new door openings		Low	Form new opening as part of re-planning of interiors	New doors and frames to be of their time to avoid confusion about provenance	Low

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.002	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
11.003	Painted signs		High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.004	Fixed signs	警告 小心地滑 CAUTION SLIPPERY FLOOR	Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
11.005	Concrete stairs		Low	Remove and rebuild as part of re-planning of interiors	None	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.006	Flat roof		Low	Form new rooftop extension at West end to accommodate fire escape stair	Form straight joint at abutment with building 08 Ablutions Block	Low
11.007	Security screen at roof level		Low	Remove	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.008	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.009	Rainwater goods		Low	Remove embedded cast iron pipework set into wall to reduce long term maintenance burden	Record on measured survey drawings. Make good cavity.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.010	Timber doors		Low	Repair and retain	Not applicable	Neutral

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.011	Security screen and door at First Floor		Low	Remove	Record on measured survey drawings	Low
11.012	Door thresholds and plinth		Low	Retain; remove paint media from plinth and brickwork	Not applicable	Neutral

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
11.013	Metal louvres on window openings		Adverse	Remove	Not applicable	Low

### **Central Police Station**

#### 12 B Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.001	Flat roof		Moderate	Repair and retain	Avoid roof penetrations as far as possible	Low
12.002	Cells at GF level		High	Remove cells in selected locations to accommodate new North-South route across site	Record existing layout on measured survey drawings. Limit number of cells affected to the minimum necessary. Retain floor structure above. Retain remainder of cells at this level for interpretation	Moderate

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.003	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
12.004	Painted signs		High	Protect in situ	Not applicable	N/A

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.005	Fixed signs		Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A
12.006	Rainwater goods		Adverse	Replace with cast iron in pattern to match original and in correct locations	Not applicable	High

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.007	Corbelled brickwork at high level in cells		Low	Retain	Not applicable	Neutral
12.008	Barbed wire		Moderate	Remove	Record wire on measured drawings	Low

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
12.009	External walls		Moderate	Form openings in North and South walls in conjunction with new North-South route across site	Cut brickwork to form openings in North and South walls; do not re-bond brickwork.	Moderate

### **Central Police Station**

#### 13 C Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.001	External airconditioning units and other external services		Adverse	Remove	Not applicable	Moderate

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.002	Door to Ladder Store		Low	Retain	Not applicable	Neutral
13.003	Security bars at window openings		Low	Retain	Not applicable	Neutral

June 2013 Draft 11
Purcell Miller Tritton LLP

142

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.004	Flat roof		Low	Retain	Avoid roof penetrations as far as possible.	Low
13.005	Eaves detail		Low	Retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.006	Cantilever reinforced concrete canopy		Low	Retain	Not applicable	Neutral

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.007	Internal partition walls		Low	Remove as part of re- planning of interiors	Record on measured survey drawings	Low
13.008	Fixed signs		Low-High	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	N/A

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.009	Metal window frames		Moderate	Repair and retain	Not applicable	Neutral
13.010	Internal security screens		Moderate	Retain where possible	Where necessary record on measured survey drawings prior to removal	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.011	Coving at abutments between RC beams and walls		Low	Avoid penetrations for services installations as far as possible.	Cut away neatly for services penetrations and make good at abutments.	Low
13.012	Communal cells at Ground Floor		Moderate	Remove as part of re- planning of interiors	Record on measured survey drawings	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.013	Rooflight and security bars over communal cells		Moderate	Remove as part of re- planning of interiors	Record on measured survey drawings	Low
13.014	Granite threshold at external door openings		Low	Retain	Not applicable	Neutral

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
13.015	Timber boarded doors with fanlight over		Low	Repair as necessary and retain	Not applicable	Neutral
13.015	Vinyl tile floor		Adverse	Replace	Not applicable	Low

June 2013 Draft 11
Purcell Miller Tritton LLP

149

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact

### **Central Police Station**

#### 14 D Hall East Wing

Element no. Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.001 West ent Lower Gr Floor		Moderate	Retain as public entrance at this level.	Retain security gate and granite threshold. Adjust adjacent ground level as necessary to achieve barrier-free access. Pin gate back against adjacent wall in the open position if necessary.	Low

## **Central Police Station**

Element no. Description		Photo ref.	Significance	Proposal	Mitigation	Impact
head	-round ded doorway side lights		Moderate	Retain	Remove air duct and make good masonry above arch.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.003	Granite surround to cells (generally north side, alternating with brick surrounds – see next item)		Moderate	Retain door surround and gate wherever possible.	Pin back gate against wall. Remove paint media to expose granite material.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.004	Brick reveals with bull-nosed arrisses and segmental arch over (generally north side, alternating with granite surrounds – see previous item)		High	Retain door surround and gate wherever possible	Pin back gate against wall	Low

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.005	Arched opening at East end First Floor		Low	Retain as existing	Not applicable	Low
14.006	Concrete floor generally at Lower Ground Floor		Low	Excavate entire floor to install piled underpinning	Record levels on measured survey drawings. Install new floor at the same level.	Low

June 2013 Draft 11
Purcell Miller Tritton LLP

155

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.007	Part-blocked windows at Lower Ground Floor - extent of blocking varies.		Moderate	Open up window opening to full extent.	Record existing condition on measured survey drawings. Add further detail during demolition works.	Low
14.008	External granite stair from Lower Ground to Ground Floor level		Moderate	Remove stair to make way for new stair in similar position	Review design proposals to see whether existing stair can be retained.	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.009	Ashlar pattern on external walls		Moderate	Form new openings for entrance/exit to building	Set out new openings to cause minimum disruption to ashlar pattern. Record existing pattern on measured survey drawings.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.010	Blocked doorway at south-east corner		Low	Preserve blocked opening intact.	Not applicable	Neutral

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.011	Metal security gate and screen		Low	Retain insitu	Pin gate in open position if necessary	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.012	Half-round headed doorway and side lights at Ground Floor west end		Moderate	Retain insitu	Not applicable	Neutral
14.013	Structural steelwork bracing and temporary access stair		Adverse	Remove upon completion of underpinning	Not applicable	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.014	RC staircase at north-east corner		Low	Remove	Record on measured drawings	Low
14.015	Vinyl tile floor on suspended timber floor		Adverse	Remove vinyl tiles and restore boards if possible; alternatively, replace boards with new timber to match other boarded floors elsewhere on the site.	Not applicable	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.016	Cell walls at Ground Floor		Moderate	Retain insitu	Use existing door openings wherever possible. Avoid further alteration to existing altered openings where feasible.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.017	Mortuary		High	Preserve insitu	Avoid any service penetrations from adjacent spaces	Neutral
14.018	Brickwork surrounds to doorways with segmental arches over		Moderate	Increase width in selected locations to allow wheelchairs to pass	Record on measured survey drawings. Limit interventions as far as possible.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.019	Granite surrounds to doorways with lintels over		Moderate	Increase width in selected locations to allow wheelchairs to pass	Record on measured survey drawings. Limit interventions as far as possible.	Low
14.020	Flat ceilings at Ground Floor		Low	Form penetrations for services installations where necessary	Avoid disruption of beams.	Low

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.021	Arched opening at east end		Low	Retain insitu	Not applicable	Neutral

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.022	Top-lit central hall		High	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.023	Arches across central hall at First Floor		Moderate	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.024	Inset security gate and screen in First Floor cells		Low	Remove to suit new use	Remove where necessary. Record on measured drawings.	Low

### **Central Police Station**

#### 14 D Hall West Wing

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.030	Main stair		High	Remove wire mesh and framing	Record on measured drawings	Low

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.031	Brick vault over central hall at Ground Floor		High	Retain insitu	Not applicable	Neutral
14.032	Terrazzo floor in central hall at Ground floor		Moderate	Remove to enable piled underpinning	Record on measured survey drawings	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.033	Brick vaults above cells		High	Retain insitu	Avoid penetrations for services	Neutral
14.034	Cell walls (later additions)		Moderate	Remove where necessary to accommodate new cafe	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.035	Brickwork spandrels below cell windows on south side at Ground Floor		Moderate	Remove to accommodate new cafe	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.036	Cell walls flanking central hall		High	Remove to accommodate new cafe	Record on measured survey drawings. Retain selected cells for interpretation purposes.	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.037	Cell floors		Low	Remove to enable piled underpinning	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.038	Partition wall across central hall at Ground Floor		Low	Remove to accommodate new cafe	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.039	Granite pavement in cross-passage between East and West Wings		Moderate	Repair as necessary and retain insitu	Not applicable	Neutral
14.040	Granite threshold at doorway between cross- passage and East Wing		Moderate	Retain insitu	Not applicable	Neutral

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.041	Brick vault over cross-passage		High	Retain insitu	Avoid any services penetrations	Neutral
14.042	Granite floor in central hall at First Floor		Moderate	Retain insitu	Repair where necessary	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.043	Cell walls flanking central hall at First Floor		High	Retain insitu	Not applicable	Neutral
14.044	Brickwork spandrels below cell windows at Second Floor		Moderate	Remove to enable new use	Record on measured drawings. Confine changes to one elevation, north or south.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.045	Metal security screen adjacent main stair		Moderate	Retain insitu	Not applicable	Neutral

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.046	Double-height central hall at Second Floor		High	Retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.047	View ports adjacent entrance doors		Moderate	Retain insitu	Not applicable	Neutral
14.048	Services installations		Adverse	Remove	Not applicable	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.049	Metalwork and structural steel framing on exterior (typical)		Adverse	Remove	Not applicable	High
14.050	Blind arcade, south elevation		Low	Remove infill brickwork within arched openings at ground level to enable new cafe	Record on measured survey drawings. Observe and record any evidence that brickwork infills were built at the same time as the arched openings or added later	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
14.051	Blind arcade, north elevation		Low	Retain insitu	Not applicable	Neutral
14.052	Fence wall, east end of D Hall Yard		Low	Remove to reinstate access to granite stair to Lower Ground Floor level	Record on measured drawings	Low

### **Central Police Station**

#### 15 E Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.001	Dividing walls at Lower Ground Floor		Moderate	Remove to enable multi- purpose use	Record on measured survey drawings	Low
15.002	Dividing walls at Lower Ground Floor		Moderate	Remove to enable multi- purpose use	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.003	Staircase within Laundry Yard		Moderate	Remove to enable construction of Arbuthnot Wing	Record on measured survey drawings	Low

### **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.004	Services installations		Adverse	Remove	Not applicable	Moderate
15.005	Metal louvres over cell window openings		Low	Remove	Record on measured survey drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.006	Raised ground level adjacent entrance		Low	Remove to enable level access	Record on measured survey drawings	Low
15.007	Access balconies and apertures		Moderate	Retain apertures	Provide temporary closure as required for operational reasons	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.008	Central staircase		High	Retain	Provide secondary staircase within cell blocks to achieve code compliance	Low

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.009	Cell walls flanking central hall		High	Retain	Pin back cell doors against walls.	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.010	Services installations		Adverse	Remove	Not applicable	Moderate
15.011	Balcony balustrades		Moderate	Retain	Install wire net across aperture to avoid need to upgrade balustrade to meet Building Code requirements	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
15.012	Second Floor central hall		High	Retain	Not applicable	Neutral

### **Central Police Station**

#### 17 F Hall

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.001	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.002	Rainwater goods		Low	Remove existing RWPs and install new RWPs externally on North and South Elevations	Improve roof drainage to avoid ponding	Low
17.003	Exterior decorations		Adverse	Strip off and redecorate	Sample and analyse existing paint media; select new media to suit substrate and significance	High

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.004	External airconditioning units and other external services		Adverse	Remove and make good brickwork	Not applicable	High
17.005	Fixed signs	PRISONERS' PRIVATE CLOTHING STORE 犯人私家衣服儲藏室	Moderate	Remove and refix/display in visitors' centre/discard	Record each sign and assess significance individually and treat accordingly	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.006	Security screen at First Floor entrance		Low	Remove	Record on measured drawings	Low
17.007	Metal windows		Moderate	Remove at First Floor to accommodate gallery space and block structural openings with blockwork	Record on measured drawings.	Moderate

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.008	Fixed furniture		Moderate	Remove to accommodate gallery space	None	Low
17.009	Security screens		Moderate	Remove to accommodate gallery space	Record on measured drawings	Moderate

# **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.010	Timber windows		Moderate	Remove at First Floor to accommodate gallery space and block structural openings with blockwork	Record on measured drawings	Moderate
17.011	Communal washing/lavatory facilities		Moderate	Remove to accommodate gallery space	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.012	Blocked up lantern light		Low	Unblock lantern and fit glazing	Record on measured drawings	Low
17.013	Security gates at Ground openings		Moderate	Remove to enable access to Ground Floor gallery space	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.014	Interview booths		High	Remove to accommodate new gallery	Rebuild in new location	Moderate
17.015	External stair to First Floor		Moderate	Upgrade balustrade to comply with Building Code	Record on measured drawings. Supplement existing balustrade elements with minimal elements if necessary.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.016	Ground Floor main entrance		Low	Retain as existing.	Keep fixed shut if not required for operational use.	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.017	Security screen at Ground Floor main entrance		Low	Remove to accommodate gallery space	Record on measured drawings	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.018	Blue Entrance Gate (facing Old Bailey Street)		High	Retain in situ	Maintain in working order	Neutral
17.019	Blue Entrance Gate (inner) and enclosed yard		Moderate	Retain gate and enclosing walls and roof in situ; remove cupboards.	Repair and maintain gate in working order	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.020	Blue Entrance Gate (inner) facing Prison Yard		Moderate	Retain gate and enclosing frame	Repair and maintain in working order	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.021	Barbed wire		Moderate	Remove	Record on measured drawings. Make good fixing points where attached to brickwork.	Low

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.022	Metal security bars at windows		Moderate	Remove as part of blocking up window openings to accommodate gallery space at First Floor	Record on measured drawings	Low
17.023	External toilets at Ground Floor adjacent East elevation		Low	Remove	Record on measured drawings	Low

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
17.024	Open Visit Room		Low	Space reallocated to other uses	Record on measured drawings. Salvage entrance sign and re-use in new layout of interview booths.	Low

#### **19 Bauhinia House**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.001	Pitched roofs		High	New penetrations through roofs for ventilation ducts and other services	Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone.	High
19.002	Chimney		High	Repair and retain	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.003	Rainwater goods and other external services		Adverse	Remove and make good wall surface. Replace defective and non- matching rainwater goods with cast iron fittings to match original.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.004	External stone wall facing		High	Carry out close inspection of painted areas to determine extent of original granite facing and remove paint media where applicable.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.005	Gun loops		High	Remove concrete infilling and make good stonework where necessary.	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.006	Look-out turret		High	Repair and retain insitu	Not applicable	Neutral

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.007	Windows		Moderate	Remove and make good stonework as necessary	Record existing windows on measured survey drawings	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.008	Modern partitions		Adverse	Remove	Not applicable	Moderate

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.009	Electrical services		Adverse	Remove	Not applicable	Moderate
19.010	Lay-in grid suspended ceiling		Adverse	Remove	Not applicable	High

## **Central Police Station**

Element no.	Description	Photo ref.	Significance	Proposal	Mitigation	Impact
19.011	Exposed timber roof structure		High	Repair and retain insitu	Not applicable	Neutral
19.012	Timber stair		Moderate	Remove	Record on measured surveys drawings	Low
