QUARTERLY EM&A REPORT

The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: 25th Quarterly EM&A Report (1 November 2017 to 31 January 2018)

Issue Date: March 2018

Environmental Resources Management

16/F Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

QUARTERLY EM&A REPORT

The Jockey Club CPS Limited

Central Police Station Conservation and Revitalisation Project: 25th Quarterly EM&A Report (1 November 2017 to 31 January 2018)

Issue Date: March 2018

Reference 0095646

| For and on beh | alf of | |
|----------------|----------------------------------|--|
| ERM-Hong Ko | ng, Limited | |
| O | O [*] | |
| Approved by: | Frank Wan | |
| | | |
| | Warder A. | |
| Signed: | 7 | |
| <u> </u> | | |
| Position: | Partner | |
| | | |
| Certified by: | 2 | |
| | onmental Team Leader – Katie Yu) | |
| ` | , | |
| Date: | 1 March 2018 | |

This report has been prepared by ERM-Hong Kong, Limited with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client.

We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.

This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.



Your ref. 0095646 let Atkins 20180410 Quarterly EM&A Report No.25.doc

Our ref. 5121189/17.20/OC137/KC/EK

Date: 24 April 2018

香港九龍尖沙咀海港城 九倉電訊中心十三樓 13/F Wharf T&T Centre Harbour City Tsim Sha Tsui Kowloon Hong Kong

電話 Tel (852) 2972 1000 傳真 Fax (852) 2890 6343

info.hk@atkinsglobal.com www.atkinsglobal.com

By Post and Email (katie.yu@erm.com)

ERM-Hong Kong Limited, 16/F Berkshire House, 25 Westlands Road, Quarry Bay, Hong Kong

Attn: Ms Katie Yu

Dear Katie,

Central Police Station Conservation and Revitalization Project Verification of Quarterly EM&A Report No. 25

We refer to your letter dated 10 April 2018 regarding the Quarterly EM&A Report No. 25. Atkins China Limited verifies, in the capacity of Independent Environmental Checker, that the report conforms the requirements provided in Section 10.4 of the EM&A Manual.

Yours sincerely, For Atkins China Limited

Keith Chau

Independent Environmental Checker

c.c. HKJC – Mr. Kenneth Lee (By Email)
Rocco Design Architect – Mr. Charles Kung (By Email)

CONTENTS

| | EXECUTIVE SUMMARY | 1 |
|------------------------|--|----|
| 1 | INTRODUCTION | 1 |
| 1.1 | PURPOSE OF THE REPORT | 1 |
| 1.2 | STRUCTURE OF THE REPORT | 1 |
| 2 | PROJECT INFORMATION | 3 |
| 2.1 | BACKGROUND | 3 |
| 2.2 | SITE DESCRIPTION | 3 |
| 2.3 | CONSTRUCTION ACTIVITIES | 3 |
| 2.4 | CONSTRUCTION PROGRAMME | 4 |
| 2.5 | PROJECT ORGANISATION AND MANAGEMENT STRUCTURE | 4 |
| 2.6 | STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS | 4 |
| 3 | ENVIRONMENTAL MONITORING REQUIREMENTS | 6 |
| 3.1 | NOISE MONITORING | 6 |
| 3.2 | CULTURAL HERITAGE | 7 |
| 3.3 | LANDSCAPE AND VISUAL MONITORING | 9 |
| 3.4 | ENVIRONMENTAL REQUIREMENTS IN CONTRACT DOCUMENTS | 9 |
| 4 | IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES | 10 |
| 5 | MONITORING RESULTS | 11 |
| 5.1 | Noise | 11 |
| 5.2 | LANDSCAPE AND VISUAL MONITORING | 11 |
| 5.3 | CULTURAL HERITAGE | 14 |
| 5.4 | WASTE MANAGEMENT | 15 |
| 5. 4 5.5 | EFFECTIVENESS OF MITIGATION MEASURES AND MONITORING | 16 |
| <i>3.3</i> | | 10 |
| 6 | ENVIRONMENTAL SITE INSPECTION | 17 |
| 7 | ENVIRONMENTAL NON-CONFORMANCE | 19 |
| 8 | REVIEW OF THE EM&A DATA AND EIA PREDICTIONS | 21 |
| 8.1 | NOISE | 21 |
| <i>8</i> .2 | WASTE MANAGEMENT | 21 |
| 8.3 | SUMMARY OF REVIEW | 22 |
| 9 | CONCLUSIONS | 23 |

LIST OF TABLES

| Table 2.1 | Summary of Construction Activities undertaken in this Reporting Period |
|-----------|---|
| Table 2.2 | Summary of Environmental Licensing, Notification and Permit Status |
| Table 3.1 | Construction Phase Noise Monitoring Locations |
| Table 3.2 | Noise Monitoring Equipment |
| Table 3.3 | Action and Limit Levels for Construction Noise Monitoring |
| Table 3.4 | Alert, Alarm and Action (AAA) Levels for Vibration Monitoring |
| Table 3.5 | Event and Action Plan for vibration monitoring |
| Table 4.1 | Status of Required Submissions |
| Table 5.1 | Findings of Monthly Tree Inspection in the Reporting Period |
| Table 5.2 | Quantities of Waste Generated from the Project |
| Table 8.1 | Comparison of Construction Noise Standard and Noise Monitoring Results |
| Table 8.2 | Quantity of Actual Amount of C&D Materials, General Wastes and Chemical |
| | Wastes Generated and EIA Estimation |
| | |

LIST OF ANNEXES

| Annex A | Locations of Works Areas and the Surroundings |
|----------|--|
| Annex A1 | Project Location |
| Annex A2 | Declared Monuments within the Project Site |
| Annex A3 | Site Layout Plan marked with Works |
| Annex B | Project Organization Chart and Contact Detail |
| Annex C | Locations of Noise Monitoring Stations and Noise Sensitive Receivers |
| Annex D | Monitoring Schedule of the Reporting Period |
| Annex E | Calibration Reports for Calibrators and Sound Level Meters |
| Annex F | Event/Action Plans for Noise |
| Annex G | Summary of Implementation Status |
| Annex H | Noise Monitoring Results |
| Annex I | Construction Programme of the Project |
| Annex J | Waste Flow Table |
| Annex K | Environmental Complaint, Environmental Summons and Prosecution Log |
| Annex L | Records of Vibration Monitoring for Other Construction Works |
| Annex M | Summary of Condition of Character Defining Elements, Historic Buildings and Structures |

EXECUTIVE SUMMARY

The construction works of **Central Police Station Conservation and Revitalisation Project** commenced on 24 October 2011. This is the 25th quarterly Environmental Monitoring and Audit (EM&A) summary report presenting the EM&A works carried out during the period from 1 November 2017 to 31 January 2018 in accordance with the EM&A Manual.

Environmental Monitoring and Audit Progress

A summary of the monitoring activities undertaken in this reporting period is listed below:

| • | Construction Noise Monitoring during normal weekdays at | |
|---|---|----------|
| | each monitoring station | 16 times |
| • | Joint Environmental Site Inspection | 3 times |
| • | Heritage Site Inspection | 76 times |
| • | Landscape & Visual Monitoring / tree inspection | 3 times |
| • | Vibration monitoring for other construction works | 76 times |
| | | |

Noise

16 sets of 30-minute construction noise measurements were carried out at each of the monitoring stations (NM2 and NM6) during normal weekdays of the reporting period.

Due to access issue to Chancery Mansion (NM6) on 22 November 2017, noise monitoring was conducted on the ground floor of NM6 instead. Access issue was later resolved and the subsequent noise monitoring (i.e. 28 November 2017) was resumed at the rooftop of NM6.

No exceedance of the Limit Level of construction noise was recorded during the reporting period. The Action Level of construction noise (complaint received) was triggered once during the reporting period.

Cultural Heritage

No vibration monitoring was carried out for demolition works, trial piling or pile/bored piling works as the aforementioned works were not conducted during the reporting period.

Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

• 76 vibration monitoring measurements for the structural addition and alteration works at Block 11.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

76 heritage site inspections were conducted and the Contractor has generally implemented the necessary protection measures as recommended.

Landscape & Visual

Landscape and visual monitoring has commenced since October 2011 on a monthly basis. Three monthly tree inspections have been conducted by the arborist during the reporting period. The recommended actions have been performed by the Contractor as advised in the reporting period.

Waste Management

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. 266.17 tonnes of inert C&D materials and 422.57 tonnes of non-inert C&D materials were generated during the reporting period. 1,882 kg of paper/cardboard packaging was recycled during the reporting period. No metal or plastics waste was recycled during the reporting period. No chemical waste was collected by licenced chemical waste collector during the reporting period.

Environmental Site Inspection

Three joint environmental site inspections were carried out by the representatives of the Contractor, the IEC and the ET during the reporting period. Key observations and recommendations identified during the monthly site inspections were rectified by the Contractor in the subsequent monthly site inspections.

Environmental Exceedance/Non-conformance/Compliant/Enquiry/ Summons and Prosecution

No exceedance of the Limit Level of construction noise was recorded at designated monitoring stations during the reporting period. The Action Level of construction noise (complaint received) was triggered once during the reporting period.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

No enquiry was received during the reporting period.

No environmental non-compliance event was recorded during the reporting period. No non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period.

Two complaints were received during the reporting period.

No summons/prosecution was received in this reporting period.

1 INTRODUCTION

ERM-Hong Kong, Limited (ERM) was appointed by the Jockey Club CPS Limited (the CPS Ltd) as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the **Central Police Station Conservation and Revitalisation Project** (the Project).

1.1 Purpose of the Report

This is the 25th quarterly EM&A summary report, which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from 1 November 2017 and 31 January 2018.

1.2 STRUCTURE OF THE REPORT

The structure of the report is as follows:

Section 1: **Introduction**

details the scope and structure of the report.

Section 2: **Project Information**

summarises background and scope of the Project, site description, project organization and contract details, construction programme, the construction works undertaken and the status of Environmental Permit(s)/License(s) during the reporting period.

Section 3: Environmental Monitoring Requirements

summarises the monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event/Action Plans, environmental mitigation measures as recommended in the EIA report, and relevant environmental requirements.

Section 4: **Implementation Status on Environmental Mitigation Measures** summarises the implementation of environmental protection measures during the reporting period.

Section 5 : **Monitoring Results**

summarises the monitoring and waste management results obtained in the reporting period.

Section 6: Environmental Site Inspection

summarises the audit findings of the monthly site inspections undertaken within the reporting period.

Section 7: **Environmental Non-conformance** summarises any monitoring exceedance, environmental complaints and environmental summons received within the reporting period.

Section 8 : **Review of the EM&A Data and EIA Predictions** compares the monitoring data and waste quantity against predictions in the approved Project EIA report.

Section 9: Conclusions

2 PROJECT INFORMATION

2.1 BACKGROUND

The Chief Executive (CE)'s 2007-2008 Policy Address highlighted revitalisation as the guiding principle of heritage conservation and the Project was among one of the specific proposals put forward by the CE in the same Policy Address. At the meeting of the Executive Council (ExCo) on 15 July 2008, the ExCo advised and the CE ordered that Government should enter into a partnership with the Hong Kong Jockey Club (HKJC) in the form of an agreement (or agreements) to take forward the conservation and revitalisation of the CPS project based on various guiding parameters. The Project is now being undertaken in partnership with the Development Bureau of the HKSAR Government. The HKJC has taken on board the decision at the ExCo meeting and further investigated the design and implementation of the Project. The Project is now implemented by the Jockey Club CPS Limited.

2.2 SITE DESCRIPTION

The location of the Project Site is shown in *Annex A1*. The Site is bounded by Hollywood Road to the north, Arbuthnot Road to the east, Chancery Lane to the south and Old Bailey Street to the west.

The Site comprises three Declared Monuments designated under the *Antiquities and Monuments Ordinance* in 1995. They are:

- Central Police Station;
- Former Central Magistracy; and
- Victoria Prison Compound.

They are collectively named the Central Police Station (CPS). *Annex A2* shows the location of the Declared Monuments within CPS and the buildings within the CPS.

2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in this reporting period is shown in *Table 2.1* and illustrated in *Annex A3*.

Table 2.1 Summary of Construction Activities undertaken in this Reporting Period

Construction Activities Undertaken

November 2017:

- Sitewide hard landscape construction;
- Timber elements repair and replacement at Blocks 3, 9, 10 and 14;
- Fitting out works at Blocks 3, 8, 9, 10, 11, 12, 13, 14, 17 and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 8, 9, 10, 12, 13, 14 and 15;
- External façade repair at Blocks 1, 3, 9, 10, 12, 13, 14, 17 and 19;
- E&M fixing at Blocks 1, 3, 6, 7, 9, 12, 13, 14, 15, Arbuthnot Wing and Old Bailey Wing;
- Footbridge construction; and
- Structural enhancement works at Blocks 3, 8, 9, 10 and 14.

December 2017:

- Sitewide hard landscape construction;
- Timber elements repair and replacement at Blocks 3, 9, 10 and 14;
- Fitting out works at Blocks 1, 3, 9, 10, 11, 12, 13, 14, 17 and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 9, 10, 12 and 14;
- External façade repair at Blocks 3, 9, 10, 12, 13, 14, 17 and 19;
- E&M fixing at Blocks 1, 3, 6, 7, 9, 12, 13, 14, 15, Arbuthnot Wing and Old Bailey Wing;
- Footbridge construction; and
- Structural enhancement works at Blocks 3, 8, 9, 10 and 14.

January 2018:

- Sitewide hard landscape construction;
- Timber elements repair and replacement at Blocks 3, 9, 10 and 14;
- Fitting out works at Blocks 1, 3, 9, 10, 11, 12, 14, 17 and Old Bailey Wing;
- Metal works repair at Blocks 1, 3, 6, 9, 10, 12, 14, 15, 17, 19;
- External façade repair at Blocks 3, 9, 10, 13 and 14;
- E&M fixing at Blocks 1, 3, 9, 10, 13, 14, Arbuthnot Wing and Old Bailey Wing;
- Footbridge construction; and
- Structural enhancement works at Blocks 1, 3, 8, 9, 10 and 14.

2.4 CONSTRUCTION PROGRAMME

The most updated construction programme for the Project is presented in *Annex I*.

2.5 PROJECT ORGANISATION AND MANAGEMENT STRUCTURE

The Project organization chart, hotline number and contact details are shown in *Annex B*.

2.6 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the valid permits, licences, and/or notifications on environmental protection for this Project within the reporting period is presented in *Table 2.2*.

Table 2.2 Summary of Environmental Licensing, Notification and Permit Status

| Permit/ Licences/ Notification | Reference | Validity Period | Remarks |
|--|---|--|--|
| Environmental Permit (EP) | EP-408/2011/C | Throughout the Contract | Permit granted on 29 April 2016 |
| Notification of Construction Works as required under <i>Air</i> Pollution Control (Construction Dust) Regulation | Ref. No. 332920 | Throughout the Contract | - |
| Registration of Chemical Waste Producer under <i>Waste</i> <i>Disposal Ordinance</i> | Chemical Waste Producer No.: 5213- 122-G2347-25 | Throughout the Contract | - |
| Disposal of C&D material/waste | Billing Account Number: 7013338 | Throughout the Contract | - |
| Effluent Discharge License under Water Pollution Control Ordinance | License No. WT00026824-2017 | 11 Jan 2017 - 31 Oct 2021 | - |
| Notification of Commencement of Asbestos Abatement Work under Air Pollution Control Ordinance | - | Throughout the Contract | EPD's letter (EPD's ref.: (5) in EPAC/A/4/000/23 3 II) dated 2 December 2011 satisfied that the content of the asbestos abatement plan (Report No.: 0210/11/ED/0078A) is in accordance with the APCO |
| Approval of Asbestos Abatement Work (Phase 2) | - | Earliest commencement date on 26 January 2012 | EPD's letter (EPD's ref:() in EPAC/A/4/000/23 3) dated 18 January 2012. |
| Construction Noise Permit (CNP) | GW-RS0980-17 | 15 November 2017 at 1900 hours to 14 May 2018 at 2300 hours | - |
| | GW-RS0983-17 | 15 November 2017 at 2300 hours to 30 January 2018 at 0600 hours | - |

3

3.1 Noise Monitoring

3.1.1 Monitoring Location

The construction noise monitoring locations are given in *Table 3.1* and shown in *Annex C*.

 Table 3.1
 Construction Phase Noise Monitoring Locations

| Monitoring Location | Proposed Construction Noise Monitoring Station | | | |
|--------------------------------|--|-----|------------------------|---|
| | ID in EM&A Manual | ID | Type of Measurement | Remark |
| Rooftop of Ho Fook Building | N2 | NM2 | Façade | - |
| Rooftop of Chancery Mansion | | NM6 | Façade | Accesses to the original proposed monitoring location in the EM&A Manual, Chancery House (N5), were rejected; alternative location of Chancery Mansion (N6), were therefore proposed and approved by the Authorised Person (AP), the Independent Environmental Checker (IEC) and EPD. |

The noise sensitive receivers are also shown in *Annex C*.

3.1.2 Monitoring Parameters, Frequency and Programme

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the EM&A Manual. The monitoring programme for this reporting period is shown in *Annex D*.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level (L_{eq}) in decibels dB(A). $L_{eq~(30min)}$ were used as the monitoring parameter for the time period in between 0700 – 1900 hours on normal weekdays. Supplementary information for data auditing, two statistical sound levels L_{10} and L_{90} ; the levels exceeded for 10 and 90 percent of the time respectively, were also recorded during the monitoring for reference. The measured noise levels were logged in every 5 minutes throughout the impact monitoring period.

3.1.3 Monitoring Equipment and Methodology

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures* of *Technical Memorandum on Noise from Construction Work other than Percussive Piling (GW-TM)* issued under the *Noise Control Ordinance (NCO)* (Cap 400).

The sound level meters and calibrator used for the noise measurement, as listed in *Table 3.2*, complies with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters are included in *Annex E*.

Table 3.2 Noise Monitoring Equipment

| Monitoring Stations | Monitoring Equipment (Sound Level Meter and Calibrator) |
|---------------------|---|
| NM2, NM6 | <u>Calibrator</u> CEL-120 (S/N 3421612) |
| | Sound Level Meter |
| | CEL-633A (S/N 3521757) |

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

Measurements were accepted as the calibration level from before and after the noise measurement agree to within 1.0 dB.

3.1.4 Event/Action Plan

Table 3.3 Action and Limit Levels for Construction Noise Monitoring

| Noise Monitoring Location | Action Level | $\begin{array}{c} \text{Limit Level,} \\ L_{eq(30 \text{mins}), \text{ dB(A)}} \end{array}$ | Remark |
|------------------------------|---|---|---|
| NM2, NM6 | When one documented complaint is received from any one of the sensitive receivers | 75 (note) | Applicable during 0700 – 1900 hours on normal weekdays. |

Notes:

- a) Acceptable Noise Levels for Area Sensitivity Rating of A/B/C. Limit Level is reduced to 70dB(A) for schools and 65dB(A) during school examination periods.
- b) If works are to be carried out during restricted hours, the conditions stipulated in the CNP issued by the NCA have to be followed.

The Event / Action Plan (EAP) for noise monitoring is presented in *Annex F*.

3.1.5 Mitigation Measures

The mitigation measures in accordance with the EP, EIA and EM&A Manual and their implementation status are presented in *Annex G*.

3.2 CULTURAL HERITAGE

3.2.1 *Vibration Monitoring*

In accordance with the EM&A Manual, vibration monitoring is required and the vibration control limits and vibration monitoring proposal are defined by a specialist for AMO's approval.

Baseline Monitoring

Baseline vibration monitoring was not conducted during the reporting period.

Vibration Monitoring for Demolition Works

As no demolition works were carried out, vibration monitoring for demolition works was not conducted during the reporting period.

Vibration Monitoring for Trial Piling and Pipe/Bored Piling Works

As no trial piling or pipe/bored piling works were carried out, vibration monitoring for trial piling and pipe/bored piling works was not conducted during the reporting period.

Vibration Monitoring for Other Construction Works

Vibration monitoring for specific construction works other than demolition works, trial piling works and pipe/bored piling works is also required in accordance with Building Department's requirement. The monitoring location is shown in *Annex L*. The number and location of monitoring location will depend on the location of the specific construction works. The vibration monitoring should be conducted for duration of 5 minutes on a daily basis (working day) at each vibration monitoring location.

Alert, Alarm and Action Levels

The Alert, Alarm and Action (AAA) Levels are to be implemented during the vibration monitoring and shown in *Table 3.4*.

Table 3.4 Alert, Alarm and Action (AAA) Levels for Vibration Monitoring

| Instrument Type | Item Monitored | Alert Level | Alarm Level | Action Level |
|-------------------------|------------------------|-------------|-------------|--------------|
| Vibration Monitoring | Horizontal Movement | 2.0 mm/s | 2.5 mm/s | 3.0 mm/s |

The Event / Action Plan (EAP) for vibration monitoring is shown in *Table 3.5*.

Table 3.5 Event and Action Plan for Vibration Monitoring

| Events | Action |
|----------------------------|--|
| Exceedance of Alert Level | Notify Management Contractor |
| Exceedance of Alarm Level | Notify Authorised Person/Resident Engineer |
| Exceedance of Action Level | Cease Works and submit mitigation |

3.2.2 *Mitigation Measures*

Cultural heritage mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

3.3 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, inspections of affected trees were conducted by an experienced and appropriately trained arborist. All irregularities that deviate from the recommended tree protection measures or could impose deleterious impacts on the protected trees were reported. Besides, implementation of mitigation measures for landscape and visual resources recommended in the EIA Report were also monitored during the site inspection.

3.3.1 *Mitigation Measures*

Landscape and visual mitigation measures in accordance with the EP, EIA and EM&A Manual were implemented by the Contractor and the implementation status is given in *Annex G*.

3.4 Environmental Requirements in Contract Documents

The environmental requirements as specified in the contract documents were reviewed and were covered in the EIA's requirements.

4 IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES

The Contractor has generally implemented the environmental mitigation measures (including those for archaeology) and requirements as stated in the EIA Report, EM&A Manual, EP and the contract documents. The implementation status during the reporting period is summarised in *Annex G*.

Status of required submissions under the EP during the reporting period is presented in *Table 4.1*.

Table 4.1 Status of Required Submissions

| Submission | | Submission Date |
|----------------|--|------------------|
| EP Condition | | · |
| Conditions 3.4 | • 72 nd Monthly EM&A Report | 14 November 2017 |
| | • 73rd Monthly EM&A Report | 14 December 2017 |
| | • 74th Monthly EM&A Report | 12 January 2018 |

MONITORING RESULTS

5.1 Noise

5

A total of 16 sets of 30-minute construction noise measurements were carried out at each monitoring station, NM2 and NM6, during normal weekdays of the reporting period. The monitoring results together with graphical presentations are presented in *Annex H*. The local impacts observed near the monitoring stations of NM2 and NM6 were summarised below:

- NM2: construction noise from activities in the Project Site and traffic noise from Old Bailey Street.
- NM6: construction noise from activities in the Project Site and traffic noise from Chancery Lane.

No exceedance of the Limit Level of construction noise was recorded during the reporting period. The Action Level of construction noise (complaint received) was triggered once during the reporting period.

Due to access issue to Chancery Mansion (NM6) on 22 November 2017, noise monitoring was conducted on the ground floor of NM6 instead. Access issue was later resolved and the subsequent noise monitoring (i.e. 28 November 2017) was resumed at the rooftop of NM6.

5.2 LANDSCAPE AND VISUAL MONITORING

Three monthly tree inspections were conducted by the arborist during the reporting period on 7 November 2017, 1 December 2017 and 10 January 2018 and key findings and recommendations are summarised in *Table 5.1*.

Table 5.1 Findings of Monthly Tree Inspections in the Reporting Period

| Tree No. | Botanical Name | Overall Health Condition | Arborist's Observation / Recommendations |
|-------------|-----------------------|--------------------------------|--|
| 7 Novemb | ber 2017 | | |
| Tree -5 | Mangifera indica | Fair | No further action required. |
| Tree -6 | Aleurites moluccana | Fair | • Leaves on the crown are rather sparse. |
| | | | Four pits near the planter were created for ventilation purpose for the tree. |
| | | | Tree roots were exposed from the pits; the Contractor should cover the exposed roots with hessian clothes as soon as possible. |
| | | | Keep monitoring on the growth of the tree. |
| Tree-7 | Aleurites moluccana | Fair | • Leaves on the crown are rather sparse. |
| | | | Four pits near the planter were created for ventilation purpose for the tree. |
| | | | Tree roots were exposed from the pits; the Contractor should cover the exposed roots with hessian clothes as soon as possible. |
| | | | Keep monitoring on the growth of the tree. |
| Tree-8 | Plumeria rubra | Good | No further action required. |
| Tree-9 | Araucaria cunninghami | a Good | No further action required. |
| Tree-11 | Dracaena marginata | Fair | Withered leaves were observed on the tree. |
| | | | The Contractor should closely monitor the growth of the tree especially during the nearby renovation works are in progress. |
| 1 Decemb | per 2017 | | T & |
| Tree -5 | Mangifera indica | Good | No further action required. |
| Tree -6 | Aleurites moluccana | Fair | Leaves on the crown are rather sparse. |
| | | | Four pits near the planter were created for ventilation purpose for the tree. |
| | | | Exposed roots have been wrapped with hessian clothes. |
| | | | Keep monitoring on the growth of the tree. |
| Tree-7 | Aleurites moluccana | Fair | • Leaves on the crown are rather sparse. |
| | | | Four pits near the planter were created for ventilation purpose for the tree. |
| | | | Exposed roots have been wrapped with hessian clothes. |
| | | | Keep monitoring on the growth of the tree. |
| | | | tree. |
| Tree-8 | Plumeria rubra | Good | No further action required. |

| Tree No. | | Overall Health Condition | Arborist's Observation / Recommendations |
|-------------|-----------------------|--------------------------------|---|
| Tree-11 | Dracaena marginata | Fair | Withered leaves were observed on the tree. |
| | | | The Contractor should closely monitor the growth of the tree especially during the nearby renovation works are in progress. |
| | | | Some litter was observed at the planter. The Contractor was reminded to remove the litter from the planter. |
| 10 Januar | ry 20 18 | | |
| Tree -5 | Mangifera indica | Good | No further action required. |
| Tree -6 | Aleurites moluccana | Fair | Leaves on the crown are rather sparse. |
| | | | Four pits near the planter were created for ventilation purpose for the tree. |
| | | | Some faded leaves observed due to dry season. |
| | | | Keep monitoring on the growth of the tree. |
| Tree-7 | Aleurites moluccana | Fair | • Leaves on the crown are rather sparse. |
| | | | Four pits near the planter were created for ventilation purpose for the tree. |
| | | | Some faded leaves observed due to dry season. |
| | | | Keep monitoring on the growth of the tree. |
| Tree-8 | Plumeria rubra | Good | No further action required. |
| Tree-9 | Araucaria cunninghami | a Good | No further action required. |
| Tree-11 | Dracaena marginata | Fair | Withered leaves were observed on the tree. |
| | | | The Contractor should closely monitor the growth of the tree especially during the nearby renovation works are in progress. |
| | | | Some construction debris was observed at the planter. The Contractor was reminded to remove the construction debris from the planter. |

Follow-up actions needed to be implemented were recommended to the Contractor and the status of the follow-up actions was reviewed during the subsequent monthly site inspections. Recommendations have generally been implemented by the Contractor during the reporting period.

5.3 CULTURAL HERITAGE

5.3.1 Vibration Monitoring

No vibration monitoring was carried out for demolition works, trial piling or pile/bored piling works as the aforementioned works were not conducted during the reporting period.

Other Construction Works

Vibration monitoring carried out for other construction works during the reporting period are listed below:

November 2017:

• 26 vibration monitoring measurements for the structural addition and alteration works at Block 11.

December 2017:

• 24 vibration monitoring measurements for the structural addition and alteration works at Block 11.

January 2018:

• 26 vibration monitoring measurements for the structural addition and alteration works at Block 11.

The monitoring results are presented in *Annex L*.

All monitoring results were below the Alert/Alarm/ Action Levels during the reporting period.

5.3.2 Heritage Site Audit

Heritage site audits were conducted on every working weekday by the Heritage Checker during the reporting period. Key site audit findings and recommendations are summarised below. The Contractor was urged to follow-up the necessary rectification based on the inspection findings.

2 November 2017

• It was observed that one granite threshold on ground floor of Block 14 was cut resulting in damage to the historic fabric. The Contractor was reminded to avoid further damage to the historic fabric.

6 November 2017

• Timber floorboards were observed stacking up to more than 1 meter high at Block 3 and Block 17, which may cause overloading of the floor. The Contractor was reminded to follow up.

20 November 2017

• It was observed that no protection was provided to the metal gate at Magistracy Terrace after paint removal. The metal gate was also observed to be rusted. The Contractor was reminded to remove the rust and provide sufficient protection to the historic fabric.

28 December 2017

 It was observed that workers were using inappropriate tool during paint removal at ground floor of Block 14. Brickwork was observed damaged. The Contractor was reminded to provide proper supervision for the works.

29 December 2017

• The historic screen from Block 10 was observed on the ground without protection and labelling. The Contractor was reminded to provide protection to the historic building fabric.

12 January 2018

• Debris was observed on the floor, tiles and wash basin due to paint removal on ground floor of Block 14. The Contractor was reminded to clean up the debris and protect the existing building fabric.

31 January 2018

• It was observed that a number of new metal doors at lower ground floor of Block 14 were not fabricated in accordance with approved drawings. The Contractor was reminded to rectify the doors.

No non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period. The summary of condition of the character defining elements, historic buildings and structures is contained in *Annex M*.

5.4 WASTE MANAGEMENT

Wastes generated from this Project include inert construction and demolition (C&D) materials and non-inert C&D materials. Non-inert C&D materials were made up of wastes such as general refuse and mixed construction waste. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting period are summarised in *Table 5.2*. The summary of Waste Flow Table prepared by the Contractor is shown in *Annex J.* 1,882 kg of paper/cardboard packaging was recycled during the reporting period. No metal or plastic waste was recycled during the reporting period. No chemical waste was collected by licenced chemical waste collector during the reporting period.

Table 5.2 Quantities of Waste Generated from the Project

| Month / Year | Quantity | | | | | | |
|---------------|--------------|--------------|----------|-------|----------------------|----------|--------|
| | C&D | C&D | Chemical | | Recycled materials | | |
| | Materials | Materials | Wa | ste | | | |
| | (inert) | (non-inert) | Liquid | Solid | Paper/ | Plastics | Metals |
| | (tonnes) (a) | (tonnes) (b) | (L) | (kg) | cardboard (kg) | (kg) | (kg) |
| November 2017 | 92.76 | 129.3 | 0 | 0 | 270 (c) | 0 | 0 |
| December 2017 | 86.17 | 106.77 | 0 | 0 | 1,612 ^(d) | 0 | 0 |
| January 2018 | 87.24 | 186.5 | 0 | 0 | 0 | 0 | 0 |
| Total | 266.17 | 422.57 | 0 | 0 | 1,882 | 0 | 0 |

Notes:

- (a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil. The inert C&D materials were sent to Chai Wan Public Fill Barging Point, Tuen Mun Fill Bank and Tseung Kwan O Area 137 Fill Bank.
- (b) Non-inert C&D materials include general refuse and mixed construction waste. The non-inert C&D materials were disposed of at SENT Landfill and Tseung Kwan O Area 137 Sorting Facility.
- (c) 270 kg of paper/cardboard recycling was reported by the Contractor after the submission of the monthly EM&A report for November 2017.
- (d) 1,612 kg of paper/cardboard recycling was reported by the Contractor after the submission of the monthly EM&A report for December 2017.

5.5 EFFECTIVENESS OF MITIGATION MEASURES AND MONITORING

The mitigation measures recommended in the EIA report and required by the EP are considered effective in minimising environmental impacts.

The EM&A for the Project was conducted as scheduled during the reporting period. No non-compliance events were observed during site inspections and no exceedances of limit level were recorded during the reporting period. The Action Level of construction noise (complaint received) was triggered once during the reporting period. The EM&A programme is considered effective.

6 ENVIRONMENTAL SITE INSPECTION

Three monthly environmental site inspections were conducted on 17 November 2017, 19 December 2017 and 16 January 2018 during the reporting period. There was no non-compliance recorded during the site inspections. Key observations and recommendations are summarised below. The recommendations were implemented and the observations were rectified by the Contractor in the subsequent monthly site inspection.

17 November 2017

 The lock for the chemical waste store was observed damaged. The Contractor was reminded to replace with a new lock and that the chemical waste store should be kept locked at all times.

19 December 2017

- A number of chemical drums were observed without drip tray outside Block 14. The Contractor was reminded to provide drip trays for the chemical drums;
- The Contractor was reminded to ensure all wastewater generated from the site would be treated prior to discharge to the stormwater drainage system.

16 January 2018

• Nil

This page is deliberately left blank

7 ENVIRONMENTAL NON-CONFORMANCE

7.1.1 Summary of Monitoring Exceedance

No exceedance of the Limit Level of construction noise or Alert, Alarm and Action Levels of vibration was recorded during the reporting period. The Action Level of construction noise (complaint received) was triggered once during the reporting period.

7.1.2 Summary of Enquiry

No enquiry was recorded during the reporting period.

7.1.3 Summary of Non-Compliance

No environmental non-compliance event was recorded during the reporting period. No non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period.

7.1.4 Summary of Environmental Complaint

Two complaints were received during the reporting period. The complaint investigation reports and the cumulative number of complaints are presented in *Annex K*.

7.1.5 Summary of Environmental Summons and Successful Prosecution

No summons was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex K*.

This page is deliberately left blank

8.1 NOISE

A comparison was made between the monitoring results in this reporting period and the Noise Standard for general construction works during 0700 – 1900 hrs on normal weekdays (*Table 8.1*).

Table 8.1 Comparison of Construction Noise Standard and Noise Monitoring Results

| Reporting Month | Monitoring Stations | Corresponding NSR in EIA | Noise Limit Level | Predicted Construction Noise Level (With Mitigation) in EIA | Measured Construction Noise Level |
|--------------------|------------------------|-----------------------------|-------------------------------|--|---|
| | | | L _{eq, 30 min} dB(A) | L _{eq, 30 min} dB(A) | L _{eq, 30 min} dB(A) |
| November | NM2 | N2 | 75 | 67 - 72 | 65.1 - 69.8 |
| 2017 | NM6 | N6 | 75 | 73 - 75 | 59.6 - 67.4 |
| December | NM2 | N2 | 75 | 67 - 72 | 66.3 - 69.0 |
| 2017 | NM6 | N6 | 75 | 73 - 75 | 63.7 - 73.8 |
| January 2018 | NM2 | N2 | 75 | 67 - 72 | 68.1 - 69.9 |
| | NM6 | N6 | 75 | 73 - 75 | 64.4 - 66.2 |

The monitoring results recorded since the commencement of the construction works have been below the Limit Level and comparable to the predicted construction noise level in the approved EIA. Recommended mitigation measures in *Section 5.9.1* of EIA will continue to be implemented throughout the construction stage.

8.2 WASTE MANAGEMENT

The estimated amount of waste generated in the approved EIA and the accumulated quantities of waste generated up to this reporting period are presented in *Table 8.2*. The accumulated amount of inert and non-inert C&D materials is higher than the estimated amount in EIA. The major chemical waste generated on site was primarily asbestos which was not estimated in the approved EIA and hence no data is available for comparison. Recommended mitigation measures in *Section 8.5.1* of the EIA will continue to be implemented throughout the construction stage.

Table 8.2 Quantity of Actual Amount of C&D Materials, General Wastes and Chemical Wastes Generated and EIA Estimation

| Type of Material | Estimated Amount of | Accumulated Actual Amount of | | |
|---|----------------------------|----------------------------------|--|--|
| | Waste in EIA | Waste Recorded (a) (b) | | |
| Amount of C&D Materials (Inert) Arising | 16,440 m ³ | 38,088.38 m ³ | | |
| Amount of C&D Materials (Non-inert) Arising | 890 m ³ | 16,321.50 m ³ | | |
| General Refuse | 130 kg per day | _ (c) | | |
| Chemical Waste | Less than 100L per month | - 57 L (liquid) | | |
| | | - 395 kg (solid) | | |
| | | - 7,000 kg of asbestos generated | | |

Notes:

- (a) The accumulated actual amount of C&D Materials and chemical waste were recorded since the commencement of construction works.
- (b) The volume of waste materials are provided by the Contractor based on the updated waste record in January 2018.
- (c) The amount of general refuse generated was not recorded.

8.3 SUMMARY OF REVIEW

The EIA predictions and the monitoring results since the commencement of construction works have been reviewed. The EIA concluded that the Project would not cause adverse impacts to the environment and the monitoring results have also indicated the same so far. Mitigation measures (including those for archaeology) recommended in the EP, EIA and EM&A Manual were implemented by the Contractor as far as practicable and were considered effective. The recommended mitigation measures will continue to be implemented throughout the construction phase of the Project.

The effectiveness of the monitoring programme has been exhibited therefore change to the programme is not considered to be necessary.

9 CONCLUSIONS

This 25th Quarterly EM&A Report presents the EM&A works undertaken during the reporting period from 1 November 2017 to 31 January 2018 in accordance with the EM&A Manual.

No exceedance of the Limit Level of construction noise was recorded at designated monitoring stations during the reporting period. The Action Level of construction noise (complaint received) was triggered once during the reporting period.

Tree inspections were conducted in this reporting period. Most of the necessary landscape and visual mitigation measures recommended in the EIA Report were implemented by the Contractor.

No exceedance of Alert, Alarm and Action Levels of vibration was recorded during the reporting period.

No enquiry was received during the reporting period.

No environmental non-compliance event was recorded during the reporting period. No non-compliance reports related to the character defining elements, historic buildings and structures were issued during the reporting period.


Two complaints were received during the reporting period.


No summons/prosecution was received during the reporting period.

The monitoring programme was considered effective in reflecting the environmental conditions at the designated representative sensitive receivers. The monitoring results also indicate that the Project have not caused adverse impacts on the environment with implementation of appropriate mitigation measures. Change to the monitoring programme is not considered to be necessary. The ET will keep track on the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures in the coming periods.

Annex A

Locations of Works Areas and the Surroundings

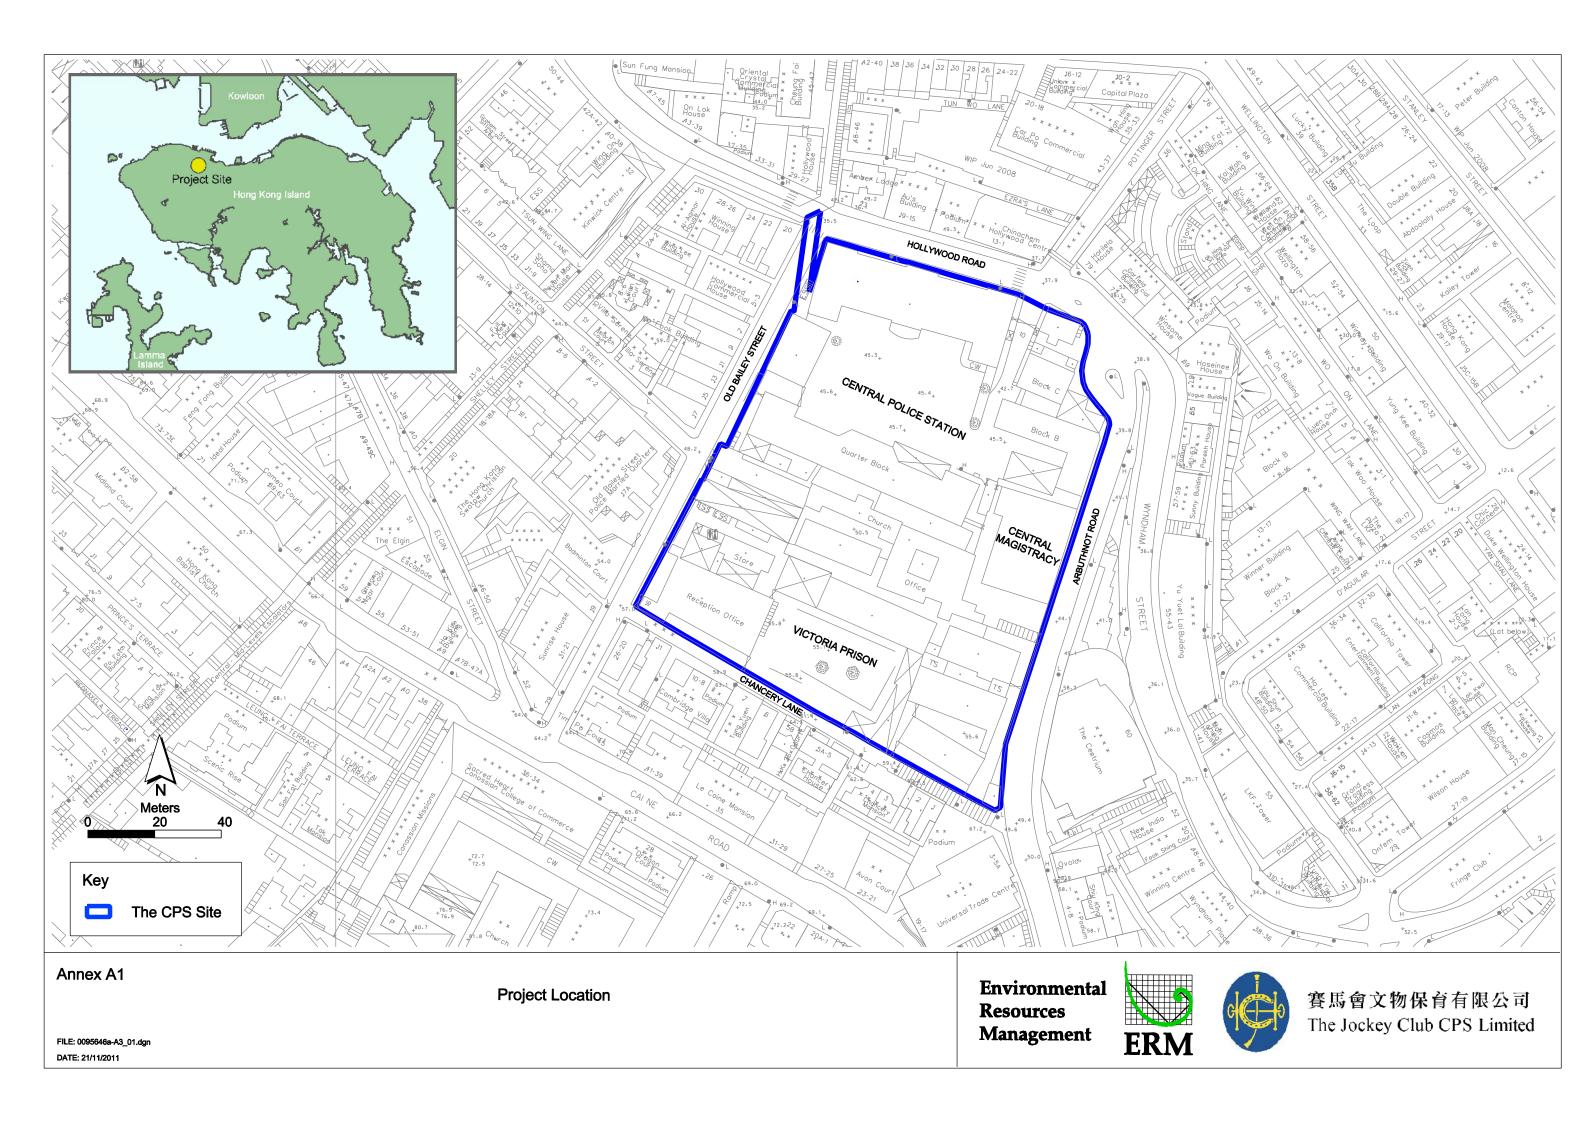

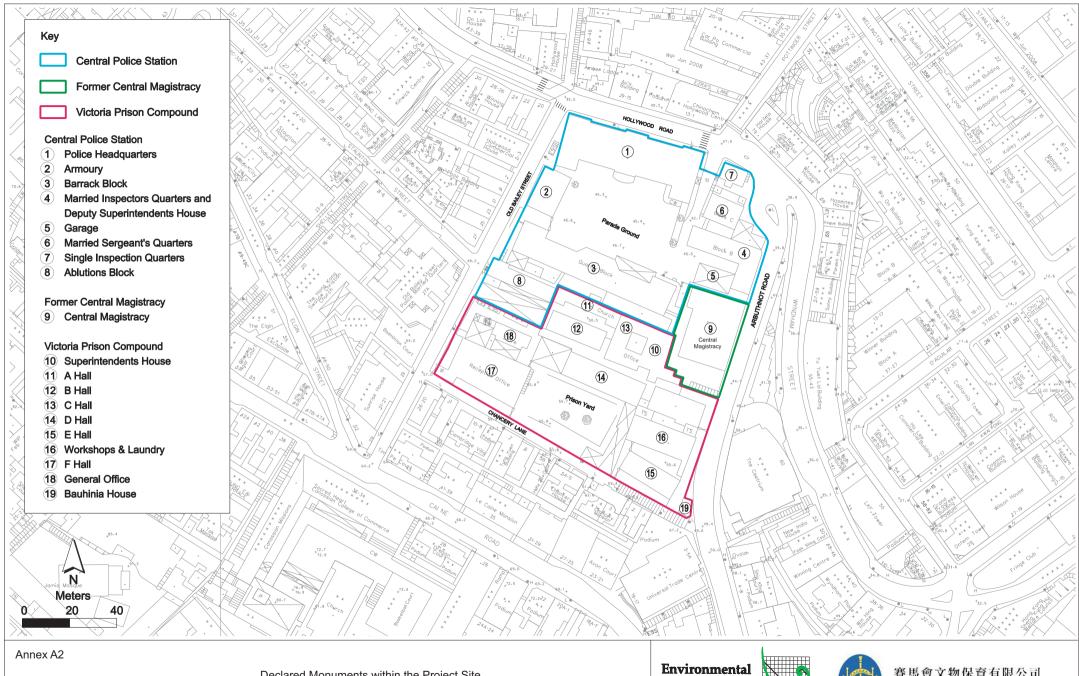


FILE: 0095646b1-A3.dgn DATE: 07/12/2011


Declared Monuments within the Project Site


Resources Management





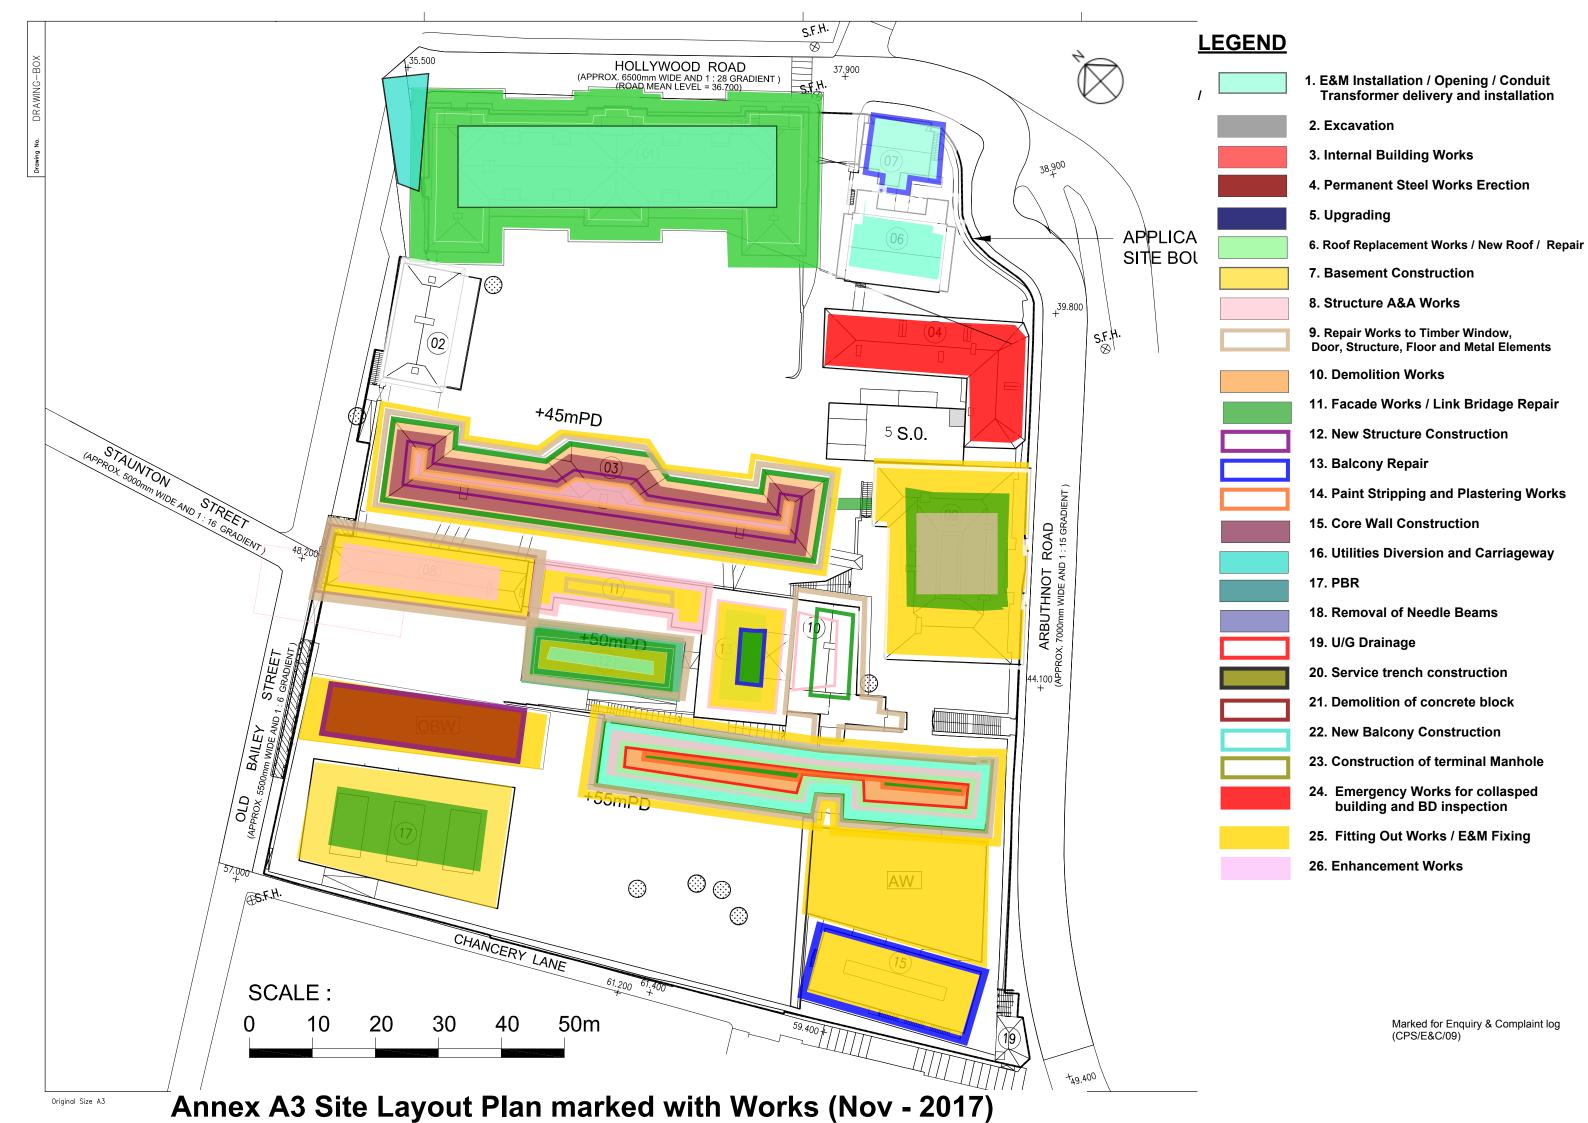


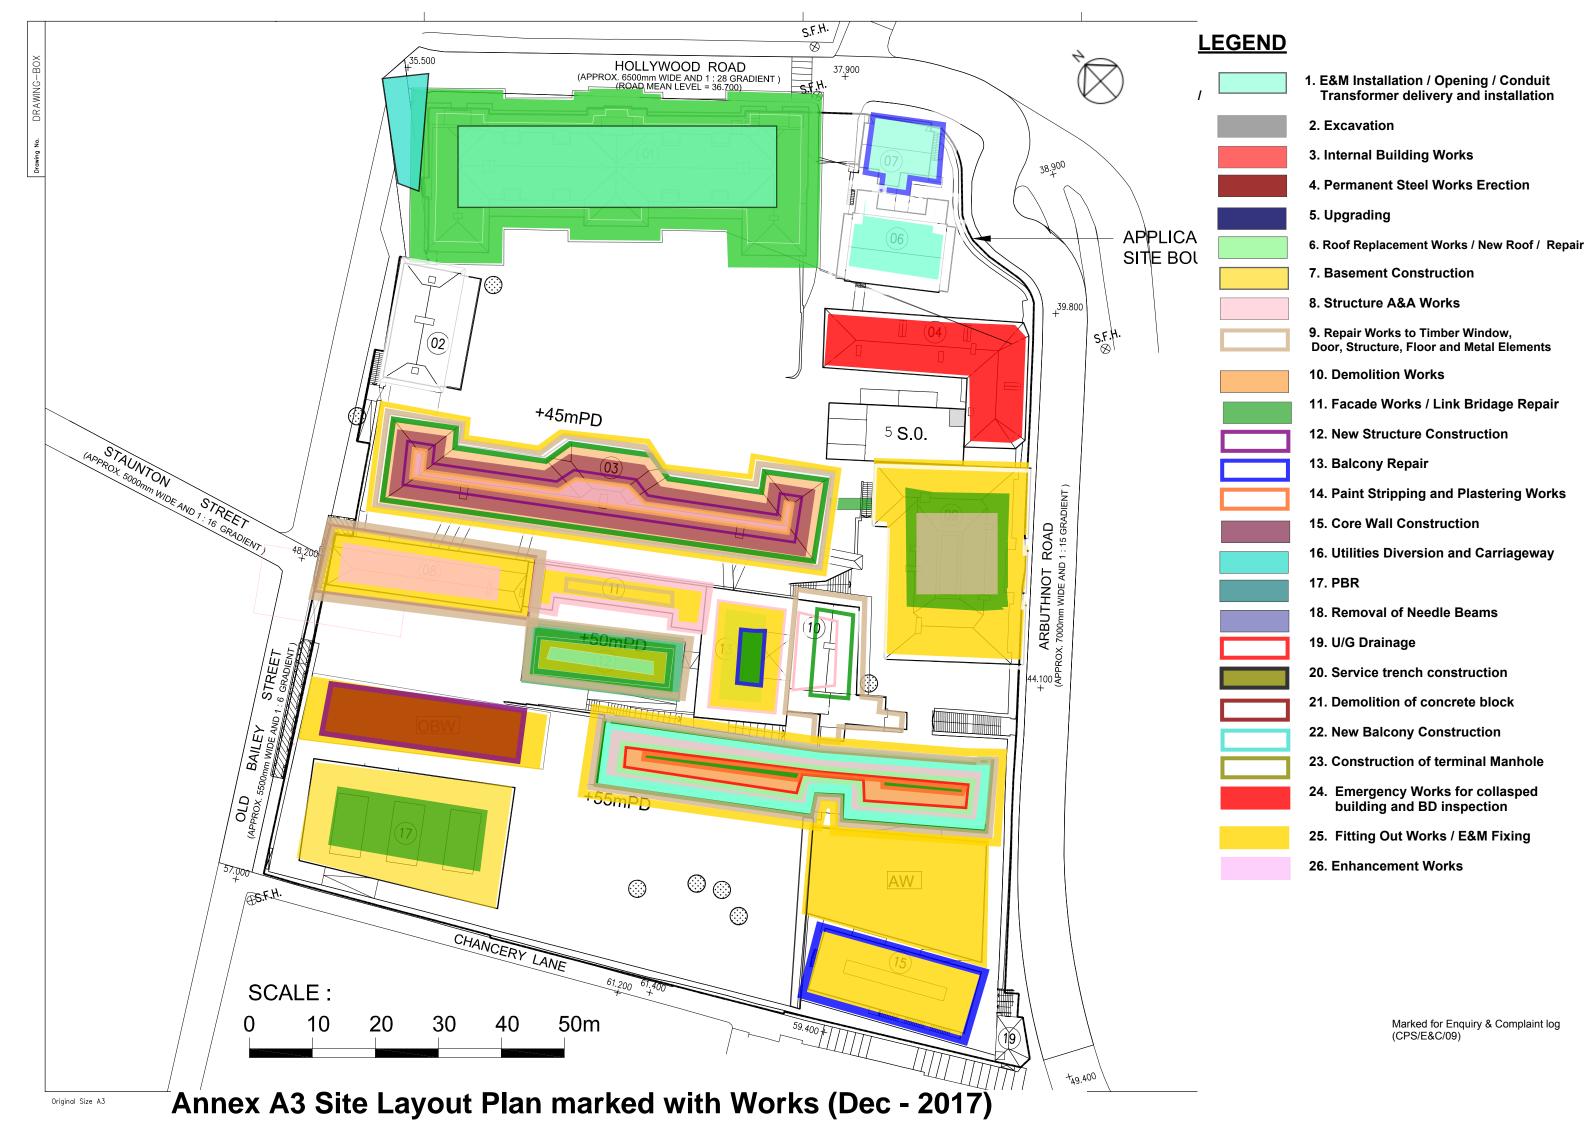

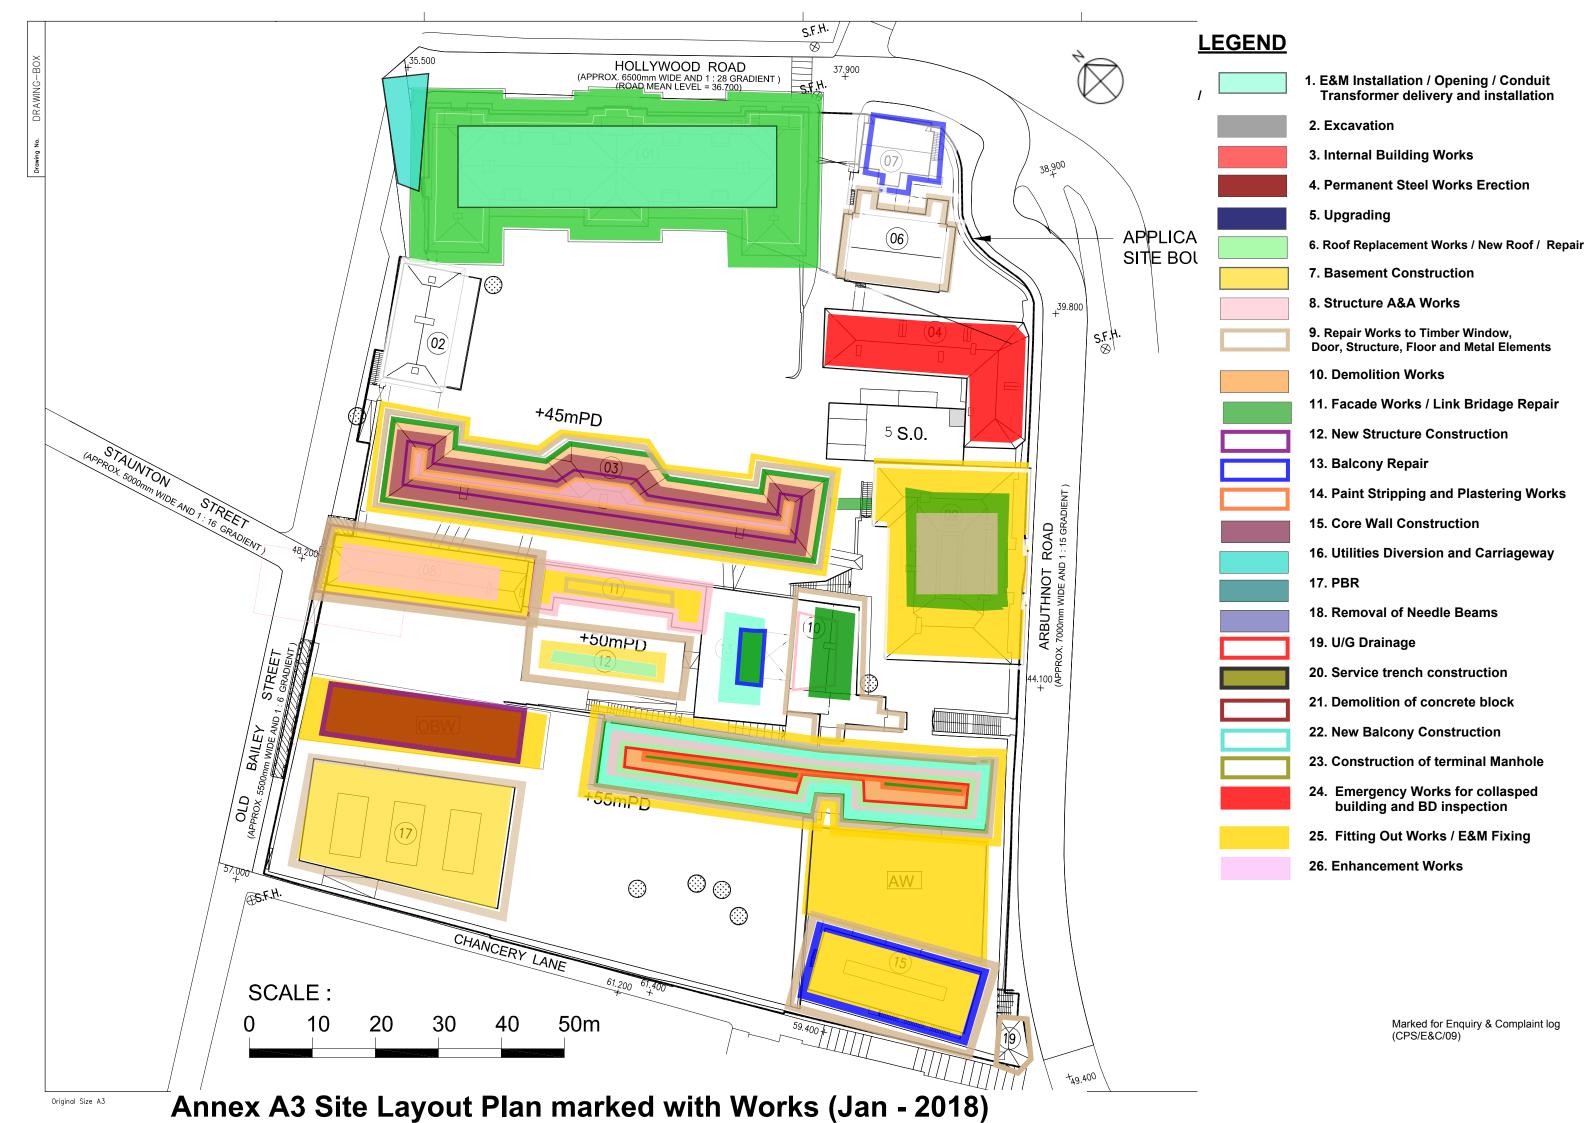


Annex B

Project Organization Chart and Contact Detail

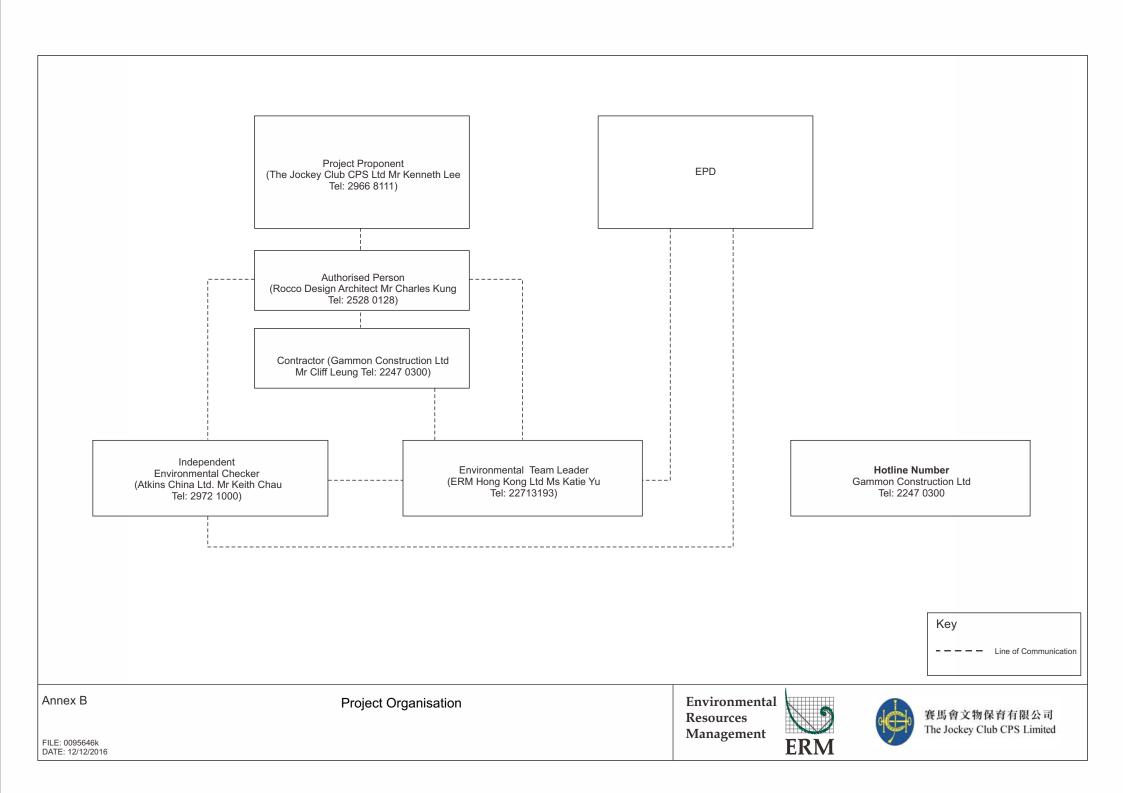

Annex C

Locations of Noise Monitoring Stations and Noise Sensitive Receivers

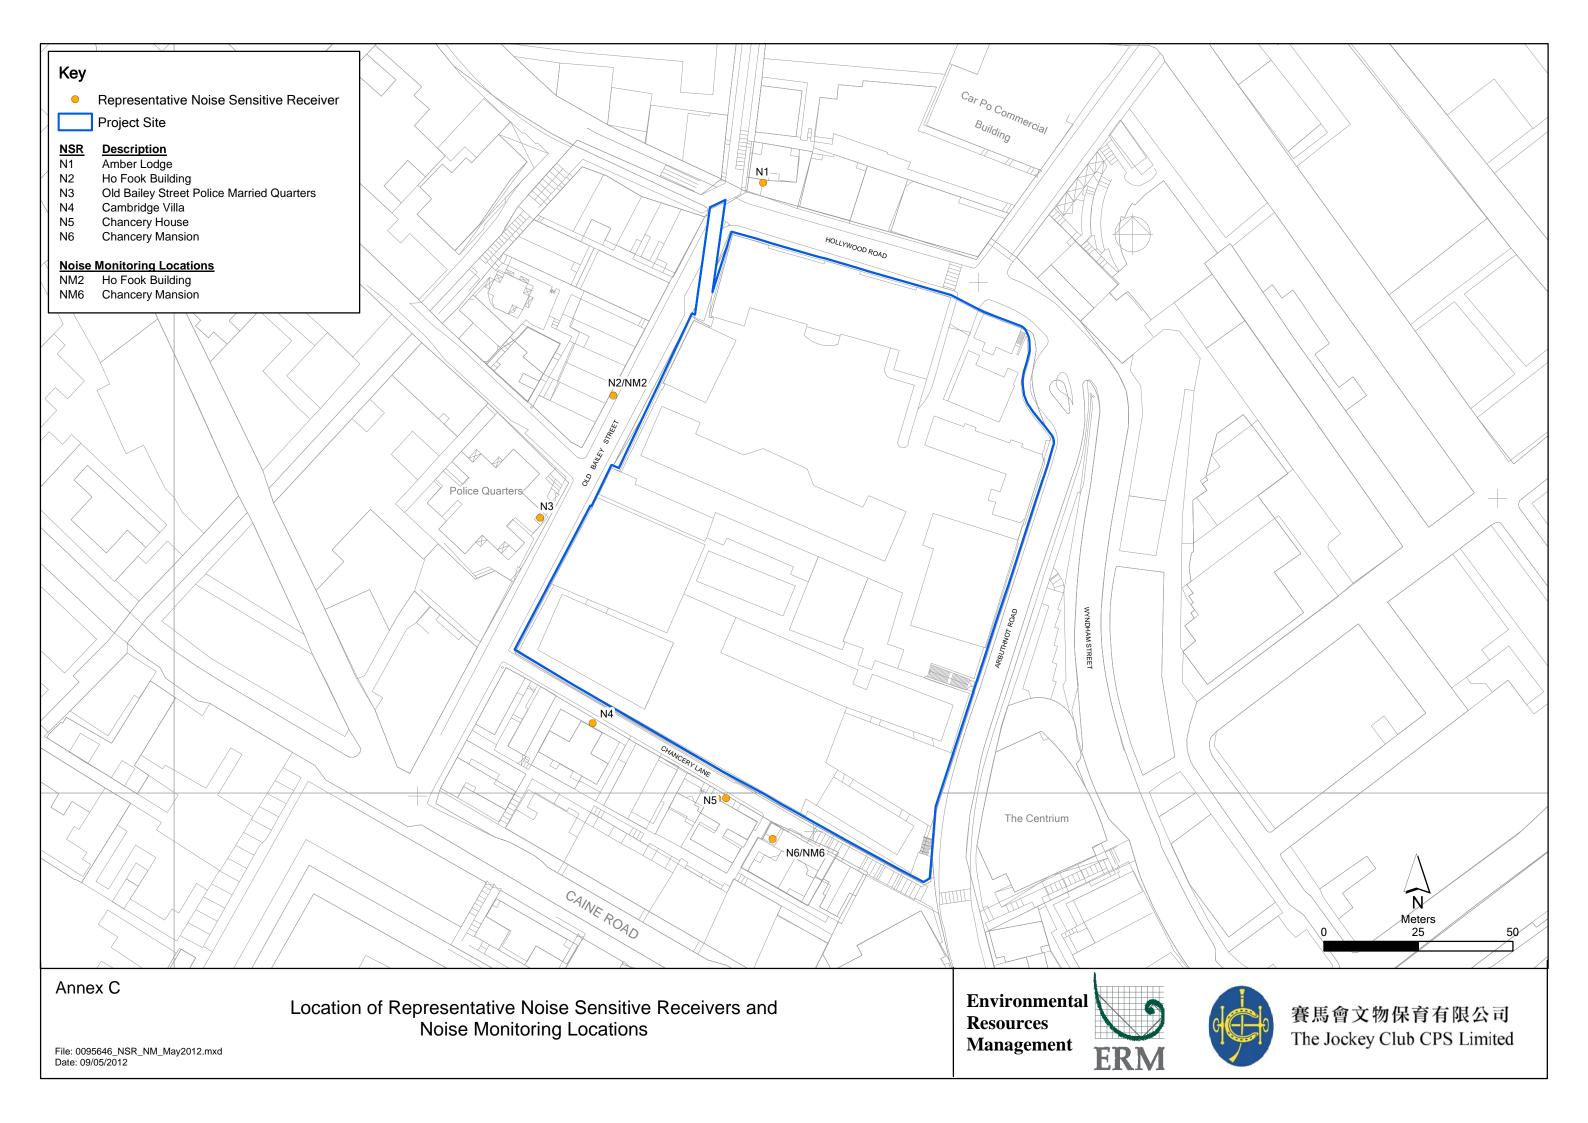

Annex D

Monitoring Schedule of the Reporting Period and Next Month

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - November 2017

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|--------|----------------------------------|----------------------------------|----------------------------------|----------------------------------|----------------------------------|----------|
| | | | 01-Nov | 02-Nov | 03-Nov | 04-Nov |
| | | | | | | |
| | | | | | | |
| | | | | | | |
| | | | | | | |
| 05-Nov | 06-Nov | 07-Nov | 08-Nov | 09-Nov | 10-Nov | 11-Nov |
| | A1 . A4 | | | | A1 . A4 | |
| | Noise Monitoring at NM2 & NM6 | | | | Noise Monitoring at NM2 & NM6 | |
| | at MINIZ & MINIO | | | | at MINZ & MINO | |
| | | | | | | |
| 12-Nov | 13-Nov | 14-Nov | 15-Nov | 16-Nov | 17-Nov | 18-Nov |
| | | | | ALC: ALC: C | | |
| | | | | Noise Monitoring at NM2 & NM6 | | |
| | | | | at INIVIZ & INIVIO | | |
| | | | | | | |
| 19-Nov | 20-Nov | 21-Nov | 22-Nov | 23-Nov | 24-Nov | 25-Nov |
| | | | Nieles Manthedre | | | |
| | | | Noise Monitoring at NM2 & NM6 | | | |
| | | | at INIVIZ & INIVIO | | | |
| | | | | | | |
| 26-Nov | 27-Nov | 28-Nov | 29-Nov | 30-Nov | | |
| | | | | | | |
| | | Noise Monitoring at NM2 & NM6 | | | | |
| | | al iniviz a inivio | | | | |
| | | | | | | |

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - December 2017

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|--------|----------------------------------|----------------|----------------------------------|----------------------------------|----------------------------------|----------------------------------|
| | | | | | 01-Dec | 02-Dec |
| | | | | | | |
| 03-Dec | 04-Dec | 05-Dec | 06-Dec | 07-Dec | 08-Dec | 09-Dec |
| | Noise Monitoring at NM2 & NM6 | | | | Noise Monitoring at NM2 & NM6 | |
| 10-Dec | 11-Dec | 12-Dec | 13-Dec | 14-Dec | 15-Dec | 16-Dec |
| | | | | Noise Monitoring at NM2 & NM6 | | |
| 17-Dec | 18-Dec | 19-Dec | 20-Dec | 21-Dec | 22-Dec | 23-Dec |
| | | | Noise Monitoring at NM2 & NM6 | | | Noise Monitoring at NM2 & NM6 |
| 24-Dec | 25-Dec | 26-Dec | 27-Dec | 28-Dec | 29-Dec | 30-Dec |
| | Public Holiday | Public Holiday | | | Noise Monitoring at NM2 & NM6 | |
| 31-Dec | | | | | | |
| | | | | | | |

Central Police Station Compound Conservation and Revitalisation (Ho Fook Building - NM2 & Chancery Mansion - NM6) Monitoring Schedule for Reporting Month - January 2018

| Sunday | Monday | Tuesday | Wednesday | Thursday | Friday | Saturday |
|--------|----------------------------------|----------------------------------|----------------------------------|----------------------------------|----------------------------------|----------|
| | 01-Jan | 02-Jan | 03-Jan | 04-Jan | 05-Jan | 06-Jan |
| | Public Holiday | | | Noise Monitoring at NM2 & NM6 | | |
| 07-Jan | 08-Jan | 09-Jan | 10-Jan | 11-Jan | 12-Jan | 13-Jan |
| | | | Noise Monitoring at NM2 & NM6 | | | |
| 14-Jan | 15-Jan | 16-Jan | 17-Jan | 18-Jan | 19-Jan | 20-Jan |
| | | Noise Monitoring at NM2 & NM6 | | | | |
| 21-Jan | 22-Jan | 23-Jan | 24-Jan | 25-Jan | 26-Jan | 27-Jan |
| | Noise Monitoring at NM2 & NM6 | | | | Noise Monitoring at NM2 & NM6 | |
| 28-Jan | 29-Jan | 30-Jan | 31-Jan | | | |
| | | | | | | |

Annex E

Calibration Reports for Calibrators and Sound Level Meters



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

1

C166691

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC16-2717) Date of Receipt / 收件日期: 28 November 2016

Description / 儀器名稱

Acoustic Calibrator

Manufacturer / 製造商

Casella

Model No. / 型號

CEL-120/1 3421612

Serial No. / 編號 Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

30 November 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By 測試

HT Wong Technical Officer

Certified By

核證

Date of Issue 簽發日期

Website/網址: www.suncreation.com

7 December 2016

Project Engineer

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C166691

S,

證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID CL130 CL281 TST150A <u>Description</u>

Universal Counter
Multifunction Acoustic Calibrator
Measuring Amplifier

Certificate No.

C163709 PA160023 C161175

4. Test procedure: MA100N.

5. Results:

5.1 Sound Level Accuracy

| Journa Dever Treeding | | | |
|-----------------------|----------------|-------------|-------------------------------|
| UUT | Measured Value | Mfr's Spec. | Uncertainty of Measured Value |
| Nominal Value | (dB) | (dB) | (dB) |
| 94 dB, 1 kHz | 94.1 | ± 0.25 | ± 0.2 |
| 114 dB, 1 kHz | 114.1 | | |

5.2 Frequency Accuracy

| requested reconstant | | | |
|----------------------|----------------|----------------------------------|-------------------------------|
| UUT Nominal Value | Measured Value | Mfr's | Uncertainty of Measured Value |
| (kHz) | (kHz) | Spec. | (Hz) |
| 1 | 1.000 0 | $1 \text{ kHz} \pm 5 \text{ Hz}$ | ± 0.1 |

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C166692

S,

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC16-2717) Date of Receipt / 收件日期: 28 November 2016

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Casella

Model No. / 型號 Serial No./編號

CEL-633A 3521757

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}$ C Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

30 November 2016

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By

測試

H T Wong

Technical Officer

Certified By

核證

K C Lee

Project Engineer

Date of Issue

7 December 2016

簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

E-mail/電郵: callab@suncreation.com

Website/網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C166692

證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration using the Casella Acoustic Calibrator CEL-120/1, S/N: 3421612 was performed before the test.
- 3. The results presented are the mean of 3 measurement at each calibration point.
- 4. Test equipment:

Equipment ID CL280 CL281

Description

Certificate No.

40 MHz Arbitrary Waveform Generator Multifunction Acoustic Calibrator C160077 PA160023

- 5. Test procedure: MA101N.
- Results:
- 6.1 Sound Pressure Level
- 6.1.1 Reference Sound Pressure Level

| UUT | Setting | Applied Value | | UUT | IEC 61672 Class 1 |
|------------------|-----------|---------------|-------|---------|-------------------|
| Time | Frequency | Level | Freq. | Reading | Spec. |
| Weighting | Weighting | (dB) | (kHz) | (dB) | - (dB) |
| L_{F} | A | 114.00 | 1 | 113.7 | ± 1.1 |

6.1.2 Linearity

| UUT | Setting | Applie | d Value | UUT |
|-------------------|------------------------|------------|----------------|--------------|
| Time Weighting | Frequency Weighting | Level (dB) | Freq. (kHz) | Reading (dB) |
| L_{F} | A | 114.00 | 1 | 113.7 (Ref.) |
| | | 104.00 | | 103.7 |
| | | 94.00 | | 93.5 |

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

| UUT | Setting | Applied Value | | UUT | IEC 61672 Class 1 | |
|-------------|-----------|---------------|-------|---------|-------------------|--|
| Time | Frequency | Level | Freq. | Reading | Spec. | |
| Weighting | Weighting | (dB) | (kHz) | (dB) | (dB) | |
| $L_{\rm F}$ | A | 114.00 | 1 | 113.7 | Ref. | |
| Ls | | | | 113.7 | ± 0.3 | |

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C166692

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

| UUT | Setting | App | lied Value | UUT | IEC 61672 Class 1 |
|-----------|-----------|-------|------------|---------|-------------------|
| Time | Frequency | Level | Freq. | Reading | Spec. |
| Weighting | Weighting | (dB) | | (dB) | (dB) |
| L_{F} | A | 94.00 | 63 Hz | 87.4 | -26.2 ± 1.5 |
| | | | 125 Hz | 97.5 | -16.1 ± 1.5 |
| | | | 250 Hz | 105.0 | -8.6 ± 1.4 |
| | | | 500 Hz | 110.4 | -3.2 ± 1.4 |
| | | | 1 kHz | 113.7 | Ref. |
| | | | 2 kHz | 114.9 | $+1.2 \pm 1.6$ |
| | | | 4 kHz | 114.6 | $+1.0 \pm 1.6$ |
| | | | 8 kHz | 112.2 | -1.1(+2.1; -3.1) |
| | | | 12.5 kHz | 108.1 | -4.3(+3.0; -6.0) |

6.3.2 C-Weighting

| UUT | Setting | Applied Value | | UUT | IEC 61672 Class 1 |
|-------------------|------------------------|---------------|----------|--------------|--------------------|
| Time Weighting | Frequency Weighting | Level (dB) | Freq. | Reading (dB) | Spec. (dB) |
| $L_{\rm F}$ | C | 94.00 | 63 Hz | 112.8 | -0.8 ± 1.5 |
| | | | 125 Hz | 113.5 | -0.2 ± 1.0 |
| | | | 250 Hz | 113.7 | 0.0 ± 1.0 |
| | | | 500 Hz | 113.7 | 0.0 ± 1.0 |
| | | | 1 kHz | 113.7 | Ref. |
| | | | 2 kHz | 113.5 | -0.2 ± 1.0 |
| | | | 4 kHz | 112.8 | -0.8 ± 1.0 |
| | | | 8 kHz | 110.4 | -3.0 (+1.5; -3.0) |
| | | | 12.5 kHz | 106.2 | -6.2 (+3.0 ; -6.0) |

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C166692

證書編號

Remarks: - UUT Microphone Model No.: CEL-251 & S/N: 1950

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 114 dB : 63 Hz - 125 Hz : \pm 0.45 dB

250 Hz - 500 Hz : $\pm 0.40 \text{ dB}$ 1 kHz : $\pm 0.30 \text{ dB}$ 2 kHz - 4 kHz : $\pm 0.45 \text{ dB}$ 8 kHz : $\pm 0.55 \text{ dB}$ 12.5 kHz : $\pm 0.80 \text{ dB}$

 $104 dB : 1 kHz : \pm 0.10 dB (Ref. 114 dB)$

94 dB : 1 kHz : \pm 0.10 dB (Ref. 114 dB)

- The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C176743

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC17-2654) Date of Receipt / 收件日期: 14 November 2017

Description / 儀器名稱

Acoustic Calibrator

Manufacturer / 製造商

Casella

Model No. / 型號 Serial No./編號

CEL-120/1 3421612

Supplied By / 委託者

Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS / 測試條件

Temperature / 溫度 :

Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓 :

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

2 December 2017

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By

測試

K C Lee

Certified By

核證

H C Chan Engineer

Date of Issue

4 December 2017

簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing I aboratory

c o 4F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax 傳真: 2744 8986 F-mail 電郵: callab a suncreation.com

Website 網址: www.suncreation.com

Page 1 of 2



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration

校正證書

Certificate No.: C176743

證書編號

The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.

2. The results presented are the mean of 3 measurements at each calibration point.

3. Test equipment:

Equipment ID

CL130

CL281 TST150A Description

Universal Counter

Multifunction Acoustic Calibrator Measuring Amplifier

Certificate No.

C173864 PA160023

C161175

4. Test procedure: MA100N.

5. Results:

Sound Level Accuracy

| UUT | Measured Value | Mfr's Spec. | Uncertainty of Measured Value |
|---------------|----------------|-------------|-------------------------------|
| Nominal Value | (dB) | (dB) | (dB) |
| 94 dB, 1 kHz | 94.0 | ± 0.25 | ± 0.2 |
| 114 dB, 1 kHz | 114.1 | | |

Frequency Accuracy

| UUT Nominal Value | Measured Value | Mfr's | Uncertainty of Measured Value |
|-------------------|----------------|----------------------------------|-------------------------------|
| (kHz) | (kHz) | Spec. | (Hz) |
| 1 | 1.000 0 | $1 \text{ kHz} \pm 5 \text{ Hz}$ | ± 0.1 |

Remark: The uncertainties are for a confidence probability of not less than 95 %.

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C176744

證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號: IC17-2654) Date of Receipt / 收件日期: 14 November 2017

Description / 儀器名稱

Sound Level Meter

Manufacturer / 製造商

Casella

Model No. / 型號 Serial No. / 編號 CEL-633A

Supplied By / 委託者

3521757 Envirotech Services Co.

Room 113, 1/F, My Loft, 9 Hoi Wing Road, Tuen Mun,

New Territories, Hong Kong

TEST CONDITIONS/測試條件

Temperature / 温度 : (23

 $(23 \pm 2)^{\circ}$ C

Relative Humidity / 相對濕度 :

 $(55 \pm 20)\%$

Line Voltage / 電壓 : --

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期

2 December 2017

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.

The results do not exceed manufacturer's specification.

The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via:

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies / Keysight Technologies
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA

Tested By

測試

K & Lee Engineer

Certified By

核證

Chan the Chan

H C Chan Engineer Date of Issue

4 December 2017

Chan 簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可測源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited - Calibration & Testing Laboratory

co 4 F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所

co香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax 傳真: 2744 8986 F-mail 電

F-mail 電郵: callab a suncreation.com

Website 網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.:

C176744

證書編號

- 1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
- 2. Self-calibration using the Casella Acoustic Calibrator CEL-120/1, S/N: 3421612 was performed before the test.
- 3. The results presented are the mean of 3 measurement at each calibration point.
- 4. Test equipment:

Equipment ID

CL280

CL281

Description

40 MHz Arbitrary Waveform Generator Multifunction Acoustic Calibrator

Certificate No. C170048

PA160023

- 5. Test procedure: MA101N.
- 6. Results:
- 6.1 Sound Pressure Level

6.1.1 Reference Sound Pressure Level

| UUT | Setting | Applie | d Value | UUT | IEC 61672 Class 1 |
|-------------------|------------------------|---------------|----------------|--------------|-------------------|
| Time Weighting | Frequency Weighting | Level (dB) | Freq. (kHz) | Reading (dB) | Spec. (dB) |
| L_{F} | A | 114.00 | 1 | 114.0 | ± 1.1 |

6.1.2 Linearity

| UUT | UUT Setting | | d Value | UUT |
|-------------------|-------------------------|------------|----------------|--------------|
| Time Weighting | Frequency Weighting | Level (dB) | Freq. (kHz) | Reading (dB) |
| L_F | L _F A 114.00 | 1 | 114.0 (Ref.) | |
| | | 104.00 | | 103.9 |
| | | 94.00 | | 93.8 |

IEC 61672 Class 1 Spec. : \pm 0.6 dB per 10 dB step and \pm 1.1 dB for overall different.

6.2 Time Weighting

| UUT | Setting Applied Value | | d Value | UUT | IEC 61672 Class 1 |
|-------------------|------------------------|------------|----------------|--------------|-------------------|
| Time Weighting | Frequency Weighting | Level (dB) | Freq. (kHz) | Reading (dB) | Spec. (dB) |
| L_{F} | A | 114.00 | 1 | 114.0 | Ref. |
| L_{S} | | | | 114.0 | ± 0.3 |

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory

本證書所載校正用之測試器材均可測源至國際標準。局部複印本證書需先獲本實驗所書面批准。

Sun Creation Engineering Limited Calibration & Testing Laboratory

cio 4 F. Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun. New Territories, Hong Kong 輝創工程有限公司 - 校正及檢測實驗所

c'o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax 傳真: 2744 8986

E-mail 電郵: callab a suncreation.com Website 網址: www.suncreation.com



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C176744

證書編號

6.3 Frequency Weighting

6.3.1 A-Weighting

| UUT | Setting | App | lied Value | UUT | IEC 61672 Class 1 |
|-------------------|------------------------|------------|------------|--------------|--------------------------|
| Time Weighting | Frequency Weighting | Level (dB) | Freq. | Reading (dB) | Spec. (dB) |
| L_{F} | A | 94.00 | 63 Hz | 87.7 | -26.2 ± 1.5 |
| | | | 125 Hz | 97.8 | -16.1 ± 1.5 |
| | | | 250 Hz | 105.3 | -8.6 ± 1.4 |
| | | | 500 Hz | 110.8 | -3.2 ± 1.4 |
| | | | 1 kHz | 114.0 | Ref. |
| | | | 2 kHz | 115.2 | $+1.2 \pm 1.6$ |
| | | | 4 kHz | 114.9 | $+1.0 \pm 1.6$ |
| | | | 8 kHz | 112.6 | -1.1(+2.1; -3.1) |
| | | | 12.5 kHz | 108.4 | - 4.3(+3.0; -6.0) |

6.3.2 C-Weighting

| UUT | Setting | App | lied Value | UUT | IEC 61672 Class 1 |
|-------------------|------------------------|------------|------------|--------------|--------------------|
| Time Weighting | Frequency Weighting | Level (dB) | Freq. | Reading (dB) | Spec. (dB) |
| L_{F} | C | 94.00 | 63 Hz | 113.2 | -0.8 ± 1.5 |
| | | | 125 Hz | 113.8 | -0.2 ± 1.0 |
| | | | 250 Hz | 114.0 | 0.0 ± 1.0 |
| | | | 500 Hz | 114.0 | 0.0 ± 1.0 |
| | | | 1 kHz | 114.0 | Ref. |
| | | | 2 kHz | 113.8 | -0.2 ± 1.0 |
| | | | 4 kHz | 113.1 | -0.8 ± 1.0 |
| | | | 8 kHz | 110.7 | -3.0 (+1.5; -3.0) |
| | | | 12.5 kHz | 106.5 | -6.2 (+3.0 ; -6.0) |

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.



Sun Creation Engineering Limited

Calibration and Testing Laboratory

Certificate of Calibration 校正證書

Certificate No.: C176744

證書編號

Remarks: - UUT Microphone Model No.: CEL-251 & S/N: 1950

- Mfr's Spec. : IEC 61672 Class 1

- Uncertainties of Applied Value : 114 dB : 63 Hz - 125 Hz : \pm 0.45 dB

250 Hz - 500 Hz : $\pm 0.40 \text{ dB}$ 1 kHz : $\pm 0.30 \text{ dB}$ 2 kHz - 4 kHz : $\pm 0.45 \text{ dB}$ 8 kHz : $\pm 0.55 \text{ dB}$

12.5 kHz : \pm 0.80 dB

 $\begin{array}{lll} 104 \ dB & : 1 \ kHz & : \pm 0.10 \ dB \ (Ref. \ 114 \ dB) \\ 94 \ dB & : 1 \ kHz & : \pm 0.10 \ dB \ (Ref. \ 114 \ dB) \\ \end{array}$

Note:

Only the original copy or the laboratory's certified true copy is valid.

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

⁻ The uncertainties are for a confidence probability of not less than 95 %.

Annex F

Event / Action Plans for Noise

Annex F Event and Action Plan for Noise

| Event | | | Ac | tion | | | |
|--------------|---|----|--|--|---|--|--|
| | Environmental Team (ET) | | dependent Environmental tecker (IEC) | A | uthorised Person (AP) | C | ontractor |
| Action Level | Notify IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, AP and Contractor; Discuss with the Contractor and formulate remedial measures; Increase monitoring frequency to check mitigation effectiveness. | 3. | Review the analysed results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the AP accordingly; Supervise the implementation of remedial measures. | 2. 3. | Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to proposed remedial measures for the analysed noise problem; Ensure remedial measures are properly implemented. | 1. | Submit noise mitigation proposals to IEC; Implement noise mitigation proposals. |
| Limit Level | Identify source; Inform IEC and AP; Repeat measurements to confirm findings; Increase monitoring frequency; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Inform IEC, AP and EPD the causes and actions taken for the exceedances; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and AP informed of the results; If exceedance stops, cease additional monitoring. | 2. | Discuss amongst AP, ET, and Contractor on the potential remedial actions; Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the AP accordingly; Supervise the implementation of remedial measures. | 1. 2. 3. 4. 5. | Confirm receipt of notification of failure in writing; Notify Contractor; Require Contractor to propose remedial measures for the analysed noise problem; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. | 1. 2. 3. 4. 5. | Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the AP until the exceedance is abated. |

Annex G

Summary of Implementation Status

Annex G Implementation Schedule for Environmental Protection Measures (1 to 30 November 2017)

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|---|---|----------|
| Cultura | al Heritag | ge | | | |
| S3.9.1 | S3.2.6 | Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO. | In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO | During detailed design and construction | √ |
| S3.9.2 | S3.3.1 | Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works. | Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road) | During detailed design and construction | √ |
| S3.9.2 | \$3.3.3 | Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed | Whole site | Prior to and during construction | ** |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|---|--|
| | | proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage. | | | |
| S3.9.3 | S3.3.4 | Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan. | Whole Site | During detailed design, construction and prior to operation | N/A – Archival recording will be conducted at later stage. |
| S3.7.3 | - | General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be | Whole site | During construction | At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------------|--------------|--|------------|---|---|
| S3.7.1 & 3.7.2 | - | checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the | Whole site | During detailed design, construction, post-construction and operation | west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4. √- CMP was implemented during the reporting month. There were no updates for the CMP. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|---|
| Landsca | пре & Visu | al | <u> </u> | I | |
| S4.7.27 | - | In-situ Tree Protection - Cordon Zone (CZ) Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ. | Whole site | During construction | The chain-link fencing for the retained trees has been removed to enable the laying of floor slab and repairing of the planters. A tree protection zone around the planter of each tree has been provided. Barricades are set up for Tree 6, 7, 8 and 9 and the barricaded zone is clear of construction materials or equipment. The vicinity of Tree 5 is also clear of construction materials or equipment. A temporary shelter has been erected around Tree 11. No major construction works in the vicinity of the trees or within the CPS site are being carried out. |
| S4.7.2 | - | In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree. | Whole site | During construction | N/A – no root pruning has been conducted yet |
| S4.7.2 | - | In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the | Whole site | During construction | N/A – The sprinkler cleansing system has been removed as major dust-generating works within the |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|--|---|--|
| | | tree or at a suitable location on an adjacent building to provide the means to wash the foliage of the accumulated dust when necessary, particularly in the dry season. | | | CPS site have been completed. |
| S4.7.2 | S4 | In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days. | Whole site | During construction | √ |
| S4.7.2 | - | Light Control Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs. | Whole site | During construction and operation | √ |
| S4.7.2 | S4 | A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil | At identified compensatory tree planting location at the Parade Ground | During detailed design and construction | √ - Planters of the compensatory trees are being built in the Parade Ground during the reporting period. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|---------------------|---|--|
| | | underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation. | | | |
| | | Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements | | | |
| | | The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department. | | | |
| S4.7.2 | S4 | Existing Granite Revetment Wall The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance. | Inner Southern Wall | During detailed design and construction | √ |
| S4.7.2 | - | New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces. | Whole site | During detailed design and construction | √ · |
| S4.7.2 | S4 | In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction. | Whole site | During post construction and operation | N/A – The quarterly inspection will be conducted at later stage. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|--------|
| S5.9 | - | The following site practices should be followed during the construction of the Project: Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. | Whole Site | During construction | |
| S5.9 | - | Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints. | Whole Site | During construction | |
| S5.9 | - | Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps. | Whole Site | During construction | √ · |
| S5.9 | - | Use quiet PME as far as practicable to mitigate the construction noise impact. | Whole Site | During construction | √ |
| S5.9 | - | Scheduling of construction activities with identified grouping of PMEs. | Whole Site | During construction | 1 |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status | | | | |
|-------------|--------------|---|------------|-------------------------------------|-----------|--|--|--|--|
| S5.11 | S5 | Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage. | Whole Site | During construction | √ · | | | | |
| Air Qu | ir Quality | | | | | | | | |
| S6.8.1 | - | Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions. | Whole Site | During construction | √ | | | | |
| S6.8.1 | - | In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time. | Whole Site | During construction | 1 | | | | |
| S6.8.1 | - | Impervious sheet will be provided for skip hoist for material transport. | Whole Site | During construction | √ | | | | |
| S6.8.1 | - | Vehicle washing facilities will be provided at the designated vehicle exit points. | Whole Site | During construction | √ | | | | |
| S6.8.1 | - | Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite. | Whole Site | During construction | √ | | | | |
| S6.8.1 | - | Road sections between vehicle-wash areas and vehicular entrances will be paved. | Whole Site | During construction | √ · | | | | |
| S6.8.1 | - | The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles. | Whole Site | During construction | 1 | | | | |
| S6.8.1 | - | Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed. | Whole Site | During construction | V | | | | |
| S6.8.1 | - | Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides. | Whole Site | During construction | √ | | | | |
| S6.8.1 | - | An effective dust screen will be provided to enclose scaffolding, if | Whole Site | During | $\sqrt{}$ | | | | |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|--|-----------------------------|-------------------------------------|---------------------|
| | | required, from the ground floor level of building for construction of superstructure of the new buildings. | | construction | |
| S6.8.1 | 1 | Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished. | Whole Site | During construction | √ |
| S6.8.1 | - | The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity. | Area for Demolition Work | During construction | √ |
| S6.8.1 | - | ULSD will be used for all construction plant on-site. | Whole Site | During construction | √ |
| S6.8.1 | - | The engine of the construction equipment or trucks during idling will be switched off. | Whole Site | During construction | V |
| S6.8.1 | - | Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions. | Whole Site | During construction | N/A – Not observed. |
| S6.10 | S3.2 | Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period. | Whole Site | During construction | √ |
| Water (| Quality | | | 1 | |
| S7.6 | - | Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly. | Whole Site | During construction | V |
| S7.6 | - | All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of. | Whole Site | During construction | N/A – Not observed. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|---------------------|
| S7.6 | - | Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system. | Whole Site | During construction | V |
| S7.6 | - | Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Waste streams classifiable as chemical wastes will be properly stored, collected and treated. | Whole Site | During construction | V |
| S7.6 | - | All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas. | Whole Site | During construction | <> |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|-----------------------------|---|------------|-------------------------------------|---------------------|
| S7.6 | - | The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters. | Whole Site | During construction | √ |
| S7.6 | - | The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals. | Whole Site | During construction | V |
| S7.6 | - | Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer. | Whole Site | During construction | V |
| S7.8 | S5.2 | Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem. | Whole Site | During construction | √ |
| | Manageme | nt | | | |
| S8.5 | S6.3.1 & Table 6.1 | General The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works. | Whole Site | During construction | V |
| S8.5 | - | Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer. | Whole Site | During construction | √ |
| S8.5 | S6.2 | A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket | Whole Site | During construction | √ |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|----------------------|--|------------|---|-----------|
| | | system will be included as one of the contractual requirements and implemented by the contractor. | | | |
| S8.5 | S6 & Table 6.1 | A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase. | Whole Site | During construction | $\sqrt{}$ |
| S8.5 | S6.3 | Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable. | Whole Site | During construction | $\sqrt{}$ |
| S8.5 | S6 | <u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD. | Whole Site | During construction and operation | V |
| S8.5 | S6 | Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. | Whole Site | During construction and operation | √ |
| S8.5 | S6 | Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and | Whole Site | During construction and operation | √ |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|----------------------|--|---|-------------------------------------|----------|
| | | Be arranged so that incompatible materials are appropriately separated. | | | |
| S8.5 | S6 | A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility. | Chemical Waste Treatment Centre at Tsing Yi | During construction and operation | V |
| S8.5 | S6 & Table 6.1 | General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts. | Whole site | During construction | √ |
| S8.5 | S6 | Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling. | Whole site | During construction and operation | √ |
| S8.5 | S6 | Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling. | Whole site | Commencement of construction | √ |
| S8.7 | S6.1 & 6.3 | Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal. | Whole site | During construction | √ |

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex G Implementation Schedule for Environmental Protection Measures (1 to 31 December 2017)

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|---|---|----------|
| Cultura | al Heritag | ge | | | |
| S3.9.1 | S3.2.6 | Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO. | In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO | During detailed design and construction | √ |
| S3.9.2 | S3.3.1 | Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works. | Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road) | During detailed design and construction | √ |
| S3.9.2 | \$3.3.3 | Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed | Whole site | Prior to and during construction | ** |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|---|--|
| | | proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage. | | | |
| S3.9.3 | S3.3.4 | Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan. | Whole Site | During detailed design, construction and prior to operation | N/A – Archival recording will be conducted at later stage. |
| S3.7.3 | - | General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be | Whole site | During construction | At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------------|--------------|--|------------|---|---|
| S3.7.1 & 3.7.2 | - | checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the | Whole site | During detailed design, construction, post-construction and operation | west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4. √- CMP was implemented during the reporting month. There were no updates for the CMP. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|---|
| Landsca | пре & Visu | al | <u> </u> | I | |
| S4.7.27 | - | In-situ Tree Protection - Cordon Zone (CZ) Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ. | Whole site | During construction | The chain-link fencing for the retained trees has been removed to enable the laying of floor slab and repairing of the planters. A tree protection zone around the planter of each tree has been provided. Barricades are set up for Tree 6, 7, 8 and 9 and the barricaded zone is clear of construction materials or equipment. The vicinity of Tree 5 is also clear of construction materials or equipment. A temporary shelter has been erected around Tree 11. No major construction works in the vicinity of the trees or within the CPS site are being carried out. |
| S4.7.2 | - | In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree. | Whole site | During construction | N/A – no root pruning has been conducted yet |
| S4.7.2 | - | In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the | Whole site | During construction | N/A – The sprinkler cleansing system has been removed as major dust-generating works within the |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|--|---|--|
| | | tree or at a suitable location on an adjacent building to provide the means to wash the foliage of the accumulated dust when necessary, particularly in the dry season. | | | CPS site have been completed. |
| S4.7.2 | S4 | In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days. | Whole site | During construction | √ |
| S4.7.2 | - | Light Control Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs. | Whole site | During construction and operation | √ |
| S4.7.2 | S4 | A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil | At identified compensatory tree planting location at the Parade Ground | During detailed design and construction | √ - Planters of the compensatory trees are being built in the Parade Ground during the reporting period. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|---------------------|---|--|
| | | underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation. | | | |
| | | Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements | | | |
| | | The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department. | | | |
| S4.7.2 | S4 | Existing Granite Revetment Wall The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance. | Inner Southern Wall | During detailed design and construction | √ |
| S4.7.2 | - | New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces. | Whole site | During detailed design and construction | √ · |
| S4.7.2 | S4 | In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction. | Whole site | During post construction and operation | N/A – The quarterly inspection will be conducted at later stage. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|--------|
| S5.9 | - | The following site practices should be followed during the construction of the Project: Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. | Whole Site | During construction | |
| S5.9 | - | Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints. | Whole Site | During construction | |
| S5.9 | - | Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps. | Whole Site | During construction | √ · |
| S5.9 | - | Use quiet PME as far as practicable to mitigate the construction noise impact. | Whole Site | During construction | √ |
| S5.9 | - | Scheduling of construction activities with identified grouping of PMEs. | Whole Site | During construction | 1 |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|-----------|
| S5.11 | S5 | Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage. | Whole Site | During construction | √ · |
| Air Qu | ality | | | | |
| S6.8.1 | - | Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions. | Whole Site | During construction | √ |
| S6.8.1 | - | In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time. | Whole Site | During construction | 1 |
| S6.8.1 | - | Impervious sheet will be provided for skip hoist for material transport. | Whole Site | During construction | √ |
| S6.8.1 | - | Vehicle washing facilities will be provided at the designated vehicle exit points. | Whole Site | During construction | √ |
| S6.8.1 | - | Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite. | Whole Site | During construction | √ |
| S6.8.1 | - | Road sections between vehicle-wash areas and vehicular entrances will be paved. | Whole Site | During construction | √ · |
| S6.8.1 | - | The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles. | Whole Site | During construction | 1 |
| S6.8.1 | - | Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed. | Whole Site | During construction | V |
| S6.8.1 | - | Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides. | Whole Site | During construction | √ |
| S6.8.1 | - | An effective dust screen will be provided to enclose scaffolding, if | Whole Site | During | $\sqrt{}$ |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|--|-----------------------------|-------------------------------------|---------------------|
| | | required, from the ground floor level of building for construction of superstructure of the new buildings. | | construction | |
| S6.8.1 | 1 | Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished. | Whole Site | During construction | √ |
| S6.8.1 | - | The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity. | Area for Demolition Work | During construction | √ |
| S6.8.1 | - | ULSD will be used for all construction plant on-site. | Whole Site | During construction | √ |
| S6.8.1 | - | The engine of the construction equipment or trucks during idling will be switched off. | Whole Site | During construction | V |
| S6.8.1 | - | Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions. | Whole Site | During construction | N/A – Not observed. |
| S6.10 | S3.2 | Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period. | Whole Site | During construction | √ |
| Water (| Quality | | | 1 | |
| S7.6 | - | Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly. | Whole Site | During construction | V |
| S7.6 | - | All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of. | Whole Site | During construction | N/A – Not observed. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|---------------------|
| S7.6 | - | Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system. | Whole Site | During construction | V |
| S7.6 | - | Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Waste streams classifiable as chemical wastes will be properly stored, collected and treated. | Whole Site | During construction | V |
| S7.6 | - | All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas. | Whole Site | During construction | V |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|-----------------------------|--|------------|-------------------------------------|---------------------|
| S7.6 | - | The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters. | Whole Site | During construction | √ |
| S7.6 | - | The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals. | Whole Site | During construction | $\sqrt{}$ |
| S7.6 | - | Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer. | Whole Site | During construction | V |
| S7.8 | S5.2 | Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem. | Whole Site | During construction | √ |
| | Manageme | ent | | | |
| S8.5 | S6.3.1 & Table 6.1 | General The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works. | Whole Site | During construction | √ |
| S8.5 | - | Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer. | Whole Site | During construction | √ |
| S8.5 | S6.2 | A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket | Whole Site | During construction | √ |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|----------------------|--|------------|---|-----------|
| | | system will be included as one of the contractual requirements and implemented by the contractor. | | | |
| S8.5 | S6 & Table 6.1 | A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase. | Whole Site | During construction | $\sqrt{}$ |
| S8.5 | S6.3 | Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable. | Whole Site | During construction | $\sqrt{}$ |
| S8.5 | S6 | <u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD. | Whole Site | During construction and operation | V |
| S8.5 | S6 | Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. | Whole Site | During construction and operation | √ |
| S8.5 | S6 | Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and | Whole Site | During construction and operation | √ |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|----------------------|--|---|-------------------------------------|----------|
| | | Be arranged so that incompatible materials are appropriately separated. | | | |
| S8.5 | S6 | A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility. | Chemical Waste Treatment Centre at Tsing Yi | During construction and operation | V |
| S8.5 | S6 & Table 6.1 | General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts. | Whole site | During construction | √ |
| S8.5 | S6 | Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling. | Whole site | During construction and operation | √ |
| S8.5 | S6 | Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling. | Whole site | Commencement of construction | √ |
| S8.7 | S6.1 & 6.3 | Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal. | Whole site | During construction | √ |

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex G Implementation Schedule for Environmental Protection Measures (1 to 31 January 2018)

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|---|---|--------|
| Cultura | al Heritag | ge | | | |
| S3.9.1 | S3.2.6 | Subject to the outcome of the archaeological investigation, if archaeological deposits are identified to be impacted by the proposed development, appropriate mitigation measures will be recommended and agreed with AMO. | In accordance with the recommendations in the Archaeological Action Plan (AAP) issued on 21 Dec 11 and approved on 30 Dec 11 by AMO | During detailed design and construction | V |
| S3.9.2 | S3.3.1 | Vibration Monitoring A baseline condition survey and baseline vibration impact will be conducted by a specialist for the approval of AMO and Buildings Department prior to commencement of the construction works to define the vibration control limits and recommend a vibration monitoring proposal for the concerned historic buildings and structures in and outside CPS for AMO's prior approval before commencement of the construction works. | Historic buildings and structures in CPS, the granite walls at Old Bailey Street and the proposed Grade 3 historic building (No. 20 Hollywood Road) | During detailed design and construction | √ |
| S3.9.2 | S3.3.3 | Compliance of the Approved Measures and Auditing Staff training by an experience building conservation expert or relevant competent person(s) in the environmental team of the project should be provided to the on-site staffs, contractors, sub-contractors and workers of the project before commencement of works to ensure their full understanding of the approved protection schedule, restoration proposal and work methodologies related to cultural heritage, and their respective responsibilities in the implementation of the environmental protection measures. Regular site audit for cultural heritage should be carried out in the construction phase by an experience building conservation expert in the environmental team ("the Heritage Checker") to investigate the site practice of the contractors and workers and their compliance of the approved work methodologies with respect of conservation works, mitigations for cultural heritage and any related works. A detailed | Whole site | Prior to and during construction | |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|---|--|
| | | proposal of the regular audit such as methodology (e.g. performance and monitoring indicators, control tools, frequency of the audit, etc.) and the conservation professionals to be engaged should be agreed with AMO prior to work commencement. The Heritage Checker shall also attend the regular site meetings with AMO and report the compliance and effectiveness of the mitigation measures for cultural heritage. | | | |
| S3.9.3 | S3.3.4 | Archival Recording An archival recording should be conducted to provide a detailed reference for the update of the Conservation Management Plan and inventory of historical features of the monuments, the preparation of asbuilt drawings showing the condition of the historic buildings and structures after the completion of the construction works. These archival records will be a reference source for future maintenance of the character defining elements, conservation of the monuments, interpretation and conservation education of the Site. The archival recording shall include but not limit to the video and photographic recording on the detailed process of the repair trials for different kinds of historical features, conservation works of character defining elements and historic fabrics of the monuments, and a written records of any new changes to the detailed design made in the construction phase illustrate with photos and drawings. A full set of the archives records (including both hard and soft copies) should be submitted to the AMO for approval after the work completion for record purpose. Any new findings related to the conservation of built heritage in the Site identified during the detailed design stage and construction phases shall be properly recorded in details for notification to the AMO and update of the Conservation Management Plan. | Whole Site | During detailed design, construction and prior to operation | N/A – Archival recording will be conducted at later stage. |
| S3.7.3 | - | General Construction Methods Prior to the commencement of the modification/refurbishment works at an existing building or structure (e.g. masonry walls near the Old Bailey Wing), a site survey will be carried out by the design team, and all building dimensions and levels of the building/structure shown will be | Whole site | During construction | At around 10:05pm on 29 May 2016, the northwest corner of Block 4 partially collapsed. The collapsed area includes northwest corner roof, west elevation façade wall, north elevation façade wall west part, 1/F and 2/F verandah west part, 2/F |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------------|--------------|--|------------|---|---|
| S3.7.1 & 3.7.2 | - | checked and confirmed by the contractor. Non-percussive piling methods will be adopted for the construction of the foundation for the new buildings. Protective and precaution measures to the existing buildings and structure adjacent to the work area (including the proposed Grade 3 historic building (No. 20 Hollywood road) and the granite boundary walls between the Ablutions Block of the police station (building no. 08) and the General Office of the prison area (building no. 18) which is adjacent to the new construction of the Old Bailey Wing and for an old granite walls at Old Bailey Street within 15m from the new construction) shall be provided to avoid damage to the existing features and to safeguard the structural integrity during the course of construction. Small scale handheld pneumatic tools with minimal vibration impact to the existing buildings/ structures are selected so as to have a better logistic and handling at the existing buildings and structures, which usually have only narrow working areas. In cases of the local demolition of structural elements, demountable platforms will be erected to temporarily support the affected area and divert the loading from above to avoid instability and create excessive cracking and settlement of the building/structure. Implementation and update of the Conservation Management Plan (CMP). Any new findings related to the conservation of the built heritage in the site identified during the detailed design and construction stage shall be properly recorded in details for the notification to the AMO and update in the CMP. After the construction, a cartographic and photographic recording on the restored historic buildings, historic features and the site shall be conducted and the following records shall be included into the CMP as appendices for updating and record purpose: • one set of measured drawings and photographic records showing the as-built condition of historic buildings and structures; and • an updated inventory list of the historic features together with the | Whole site | During detailed design, construction, post-construction and operation | west balcony, floor structure in room 04/5/03. Temporary propping has been undertaken to prevent further collapse. Construction works have resumed except Block 4. √- CMP was implemented during the reporting month. There were no updates for the CMP. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|---|
| Landsca | пре & Visu | al | <u> </u> | I | |
| S4.7.27 | - | In-situ Tree Protection - Cordon Zone (CZ) Cordon off each tree along its drip line (below the crown) with a chain-link fencing of 2.5 m height with padlocked gate, allowing limited access to area only to authorized persons. The base of the perimeter fence will be sealed up to 30 cm height to ensure that no construction drainage water will enter. If grouting is to be conducted less than 5 m from the edge of the CZ, a waterproof membrane will be installed below the ground to a depth of 1.5 m on the outer edge of the CZ to prevent the subsurface lateral movement of contaminated construction wastewater from intruding the soil inside the CZ. | Whole site | During construction | The chain-link fencing for the retained trees has been removed to enable the laying of floor slab and repairing of the planters. A tree protection zone around the planter of each tree has been provided. Barricades are set up for Tree 6, 7, 8 and 9 and the barricaded zone is clear of construction materials or equipment. The vicinity of Tree 5 is also clear of construction materials or equipment. A temporary shelter has been erected around Tree 11. No major construction works in the vicinity of the trees or within the CPS site are being carried out. |
| S4.7.2 | - | In-situ Tree Protection - Advanced & Phased Root Pruning All edges of the CZ that will be affected by excavation will undergo root pruning by a trained arborist or horticulturist, in advance of the earth work. The entire affected length of the CZ, plus 3 m additional length at both ends, shall be designated as the root pruning segment (RPS). The require trench will be opened manually in the RPS, be 1.5 m deep and 1 m wide, and closed on the same day after pruning with a good soil mix. All roots with a diameter >20 mm encountered in the course of trench opening shall be cut flushed with the inner wall of the trench. If the RPS exceeds one-quarter of the CZ circumference, the root pruning should be conducted in two stages. Each phase will tackle half of the RPS length. After the first phase, the tree will be allowed to recuperate for not less than four months before the second phase root pruning is conducted. The RPS shall be protected by sheet piles along the outer edge. The rig that installs the piles and the associated operations shall not intrude into the CZ or injure the protected tree. | Whole site | During construction | N/A – no root pruning has been conducted yet |
| S4.7.2 | - | In-situ Tree Protection - Foliage cleansing system A sprinkler cleansing system will be installed either in the crown of the | Whole site | During construction | N/A – The sprinkler cleansing system has been removed as major dust-generating works within the |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|--|---|--|
| | | tree or at a suitable location on an adjacent building to provide the means to wash the foliage of the accumulated dust when necessary, particularly in the dry season. | | | CPS site have been completed. |
| S4.7.2 | S4 | In-situ Tree Protection - Monthly inspection Monthly inspection of affected trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office. All irregularities that deviate from the recommended tree protection measures, or could impose deleterious impacts on the protected trees, must be reported to the authorized person or the tree expert within two days. | Whole site | During construction | √ |
| S4.7.2 | - | Light Control Control of night-time lighting shall be implemented to minimise impact to adjacent VSRs. | Whole site | During construction and operation | √ |
| S4.7.2 | S4 | A new planting site has been identified for compensatory tree planting in the Parade Ground. The planting is to compensate for felling of T10 and T10a. The existing tree site will be enlarged to become a wide tree strip to accommodate the compensatory trees. The entire strip of land that accommodates T1 to T4 should be revamped to improve the soil condition for future tree growth. The new tree strip should be 4 m wide and covered by porous unit pavers to permit the entry of rain and irrigation water and air exchange between the soil and the atmosphere. The unit pavers should be supported by small columns to create a vault-like structure so as to avoid compaction of the underlying soil due to pedestrian trampling. The unit pavers will be movable to provide access to the soil | At identified compensatory tree planting location at the Parade Ground | During detailed design and construction | √ - Planters of the compensatory trees are being built in the Parade Ground during the reporting period. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|---------------------|---|--|
| | | underneath so that fertilizers and conditioners could be added on a regular basis. The air conditioner unit currently located near the proposed planting site should also be removed. This new tree planting site should also be provided with proper irrigation. | | | |
| | | Pursuant to the "Environment, Transport and Works Bureau Technical Circular (Works) No. 3/2006 Tree Preservation", the compensation ratio should preferably be 1:1 according to trunk girth. An aggregate DBH of the new trees would be 60cm, the rate of compensation is beyond the requirements | | | |
| | | The replacement trees should be planted in accordance with the requirement of the landscape proposal approved by the Planning Department. | | | |
| S4.7.2 | S4 | Existing Granite Revetment Wall The inner stone face along the southern wall of the Site shall be preserved to its original historical appearance. | Inner Southern Wall | During detailed design and construction | √ |
| S4.7.2 | - | New, Patterned, High Quality, Concrete Custom Pavers should replace most of the existing paving in the open spaces. | Whole site | During detailed design and construction | √ · |
| S4.7.2 | S4 | In-situ Tree Protection - Quarterly inspection Quarterly Inspection of affected and newly planted trees by an experienced and appropriately trained arborist or horticulturist using Form 1 – Tree Group Inspection Form and Form 2 – Tree Risk Assessment Form developed by Development Bureau (http://www.trees.gov.hk/en/doc/TRAGuideline_July2010version_combine.pdf) or a form designed by a tree expert and approved by Tree Management Office for a period of 12 months after construction. | Whole site | During post construction and operation | N/A – The quarterly inspection will be conducted at later stage. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|--------|
| S5.9 | - | The following site practices should be followed during the construction of the Project: Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction phase; Silencers or mufflers on construction equipment will be utilised and will be properly maintained during the construction phase; Mobile plant, if any, will be sited as far away from NSRs as possible; Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum; Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. | Whole Site | During construction | |
| S5.9 | - | Noise insulating sheet would be adopted for certain PME (eg drill rig, excavator for demolition of existing structures, etc). The noise insulating sheet should be deployed such that there would be no opening or gaps on the joints. | Whole Site | During construction | |
| S5.9 | - | Use temporary noise barriers to mitigate the noise impact arising from the construction works, particularly for low-rise NSRs. Movable noise barriers of 3 m in height with skid footing should be used and located within a few metres of stationary plant and mobile plant such that the line of sight to the NSR is blocked by the barriers. The length of the barrier should be at least five times greater than its height. The noise barrier material should have a superficial surface density of at least 7 kg m ⁻² and have no openings or gaps. | Whole Site | During construction | √ · |
| S5.9 | - | Use quiet PME as far as practicable to mitigate the construction noise impact. | Whole Site | During construction | √ |
| S5.9 | - | Scheduling of construction activities with identified grouping of PMEs. | Whole Site | During construction | 1 |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|-----------|
| S5.11 | S5 | Weekly noise monitoring will be undertaken at the representative NSRs N2 Ho Fook Building and N5 Chancery House. Monthly site audits will be conducted to ensure that the recommended mitigation measures are properly implemented during the construction stage. | Whole Site | During construction | √ · |
| Air Qu | ality | | | | |
| S6.8.1 | - | Dust control measures stipulated in the <i>Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> will be implemented during the construction phase to control the potential fugitive dust emissions. | Whole Site | During construction | √ |
| S6.8.1 | - | In particular: Temporary stockpiles of dusty materials will be either covered entirely by impervious sheets; placed in an area sheltered on the top and three sides; or sprayed with water to maintain the entire surface wet at all the time. | Whole Site | During construction | 1 |
| S6.8.1 | - | Impervious sheet will be provided for skip hoist for material transport. | Whole Site | During construction | √ |
| S6.8.1 | - | Vehicle washing facilities will be provided at the designated vehicle exit points. | Whole Site | During construction | √ |
| S6.8.1 | - | Every vehicle will be washed to remove any dusty materials from its chassis and wheels immediately before leaving the worksite. | Whole Site | During construction | √ |
| S6.8.1 | - | Road sections between vehicle-wash areas and vehicular entrances will be paved. | Whole Site | During construction | √ · |
| S6.8.1 | - | The load carried by the trucks will be covered entirely to ensure no dust emission from the vehicles. | Whole Site | During construction | 1 |
| S6.8.1 | - | Hoarding of not less than 2.4m high from ground level will be provided along the Project Site boundary adjoining a road where the new buildings (Old Bailey Wing and Arbuthnot Wing) will be constructed. | Whole Site | During construction | V |
| S6.8.1 | - | Stockpiles of more than 20 bags of cement, dry pulverised fuel ash and dusty construction materials will be covered entirely by impervious sheeting sheltered on top and 3-sides. | Whole Site | During construction | √ |
| S6.8.1 | - | An effective dust screen will be provided to enclose scaffolding, if | Whole Site | During | $\sqrt{}$ |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|--|-----------------------------|-------------------------------------|---------------------|
| | | required, from the ground floor level of building for construction of superstructure of the new buildings. | | construction | |
| S6.8.1 | 1 | Impervious dust screen or sheeting will be implemented for demolition of structures and renovation of outer surfaces of structures that abuts or fronts open area accessible to the public to no less than 1m higher than the highest level of the structure being demolished. | Whole Site | During construction | √ |
| S6.8.1 | - | The area at which demolition work takes place will be sprayed with water or dust suppression chemical immediately prior to, during and immediately after the demolition activity. | Area for Demolition Work | During construction | √ |
| S6.8.1 | - | ULSD will be used for all construction plant on-site. | Whole Site | During construction | √ |
| S6.8.1 | - | The engine of the construction equipment or trucks during idling will be switched off. | Whole Site | During construction | V |
| S6.8.1 | - | Site practices such as regular maintenance and checking of construction equipment deployed on-site will be conducted to avoid any black smoke emissions and to minimise gaseous emissions. | Whole Site | During construction | N/A – Not observed. |
| S6.10 | S3.2 | Monthly environmental site audits to ensure that appropriate dust control measures are properly implemented and good construction site practices are adopted throughout the construction period. | Whole Site | During construction | √ |
| Water (| Quality | | | 1 | |
| S7.6 | - | Channels, earth bunds or sand bag barriers will be provided on site to direct stormwater to silt removal facilities. The design of silt removal facilities will make reference to the guidelines in <i>Appendix A1</i> of <i>ProPECC PN 1/94</i> . All drainage facilities and erosion and sediment control structures will be inspected on a regular basis and maintained to confirm proper and efficient operation at all times and particularly during rainstorms. Deposited silt and grit will be removed regularly. | Whole Site | During construction | V |
| S7.6 | - | All drainage facilities and erosion and sediment control structures will be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit will be removed regularly and disposed of. | Whole Site | During construction | N/A – Not observed. |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|--------------|---|------------|-------------------------------------|---------------------|
| S7.6 | - | Measures will be taken to reduce the ingress of stormwater into excavation areas. If the excavation of the concrete foundation is to be carried out in wet season, they will be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations will be discharged into stormwater drains via silt removal facilities. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Open stockpiles of excavated and demolition materials will be covered with tarpaulin or similar fabric during rainstorms. Measures will be taken to prevent the washing away of residues, chemicals or debris into any drainage system. | Whole Site | During construction | V |
| S7.6 | - | Manholes (including newly constructed ones) will always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Precautions will be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarised in Appendix A2 of <i>ProPECC PN 1/94</i> . Particular attention will be paid to the control of silty surface runoff during storm events. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge will be adequately designed for the controlled release of stormwater flows. All sediment traps will be regularly cleaned and maintained. The temporary diverted drainage will be reinstated to the original condition when the construction work has finished or the temporary diversion is no longer required. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Vehicle and plant servicing areas, vehicle washing bays and lubrication bays will, as far as possible, be located within roofed areas. The drainage in these covered areas will be connected to foul sewers via a petrol interceptor. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Oil leakage or spillage will be contained and cleaned up immediately. Waste oil will be collected and stored for recycling or disposal. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | Waste streams classifiable as chemical wastes will be properly stored, collected and treated. | Whole Site | During construction | V |
| S7.6 | - | All fuel tanks and chemical storage areas will be provided with locks and be sited on paved areas. | Whole Site | During construction | V |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|-----------------------------|--|------------|-------------------------------------|---------------------|
| S7.6 | - | The storage areas will be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled oil, fuel and chemicals from reaching the receiving waters. | Whole Site | During construction | √ |
| S7.6 | - | The Contractors will prepare guidelines and procedures for immediate clean-up actions following any spillages of oil, fuel or chemicals. | Whole Site | During construction | $\sqrt{}$ |
| S7.6 | - | Surface runoff from bunded areas will pass through oil/grease traps prior to discharge to the stormwater system | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | The stormwater discharge from the site will be monitored as part of the routine monitoring under the WPCO licence, if applicable. | Whole Site | During construction | N/A – Not observed. |
| S7.6 | - | The existing toilet facilities of the CPS will be available to the construction workforce. The sewage will be discharged to the public sewer. | Whole Site | During construction | V |
| S7.8 | S5.2 | Monthly site audits of the works areas will be carried out during the construction phase to monitor the environmental performance of the Project and to enable prompt actions to rectify any malpractice which may give rise to water pollution problem. | Whole Site | During construction | √ |
| | Manageme | ent | | | |
| S8.5 | S6.3.1 & Table 6.1 | General The Contractor shall apply for and obtain all the necessary waste disposal permits or licences are obtained prior to the commencement of the construction works. | Whole Site | During construction | √ |
| S8.5 | - | Management of Waste Disposal The construction contractor will open a billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities, landfills will require a valid "chit" which contains the information of the account holder to facilitate waste transaction recording and billing to the waste producer. | Whole Site | During construction | √ · |
| S8.5 | S6.2 | A trip-ticket system will also be established to monitor the disposal of construction waste at landfill and to control fly-tipping. The trip-ticket | Whole Site | During construction | √ |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|----------------------|--|------------|---|--------------|
| | | system will be included as one of the contractual requirements and implemented by the contractor. | | | |
| S8.5 | S6 & Table 6.1 | A recording system for the amount of wastes generated/recycled and disposed of will be established during the construction phase. | Whole Site | During construction | $\sqrt{}$ |
| S8.5 | S6.3 | Reduction of Construction Waste Generation C&D material will be segregated on-site into public fill and construction waste and stored in different containers or skips to facilitate reuse of the public fill and proper disposal of the construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable. | Whole Site | During construction | \checkmark |
| S8.5 | S6 | <u>Chemical Waste</u> The contractor will register as a chemical waste producer with the EPD. | Whole Site | During construction and operation | V |
| S8.5 | S6 | Containers used for storage of chemical waste shall: Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; Have a capacity of less than 450 L unless the specifications have been approved by the EPD; and Display a label in English and Chinese in accordance with instructions prescribed in <i>Schedule 2</i> of the <i>Regulations</i>. | Whole Site | During construction and operation | √ |
| S8.5 | S6 | Storage areas for chemical waste shall: Be clearly labelled and used solely for the storage of chemical waste; Be enclosed on at least 3 sides; Have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; Have adequate ventilation; Be covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and | Whole Site | During construction and operation | |

| EIA Ref. | EM&A Ref. | Recommended Mitigation Measures | Location | When to Implement the Measure | Status |
|-------------|----------------------|--|---|-------------------------------------|----------|
| | | Be arranged so that incompatible materials are appropriately separated. | | | |
| S8.5 | S6 | A licensed contractor shall be employed to collect chemical waste for delivery to a licensed treatment facility. | Chemical Waste Treatment Centre at Tsing Yi | During construction and operation | V |
| S8.5 | S6 & Table 6.1 | General Refuse General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to the transfer station, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts. | Whole site | During construction | √ |
| S8.5 | S6 | Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the Site. Materials recovered will be sold for recycling. | Whole site | During construction and operation | √ |
| S8.5 | S6 | Staff Training At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including waste reduction, reuse and recycling. | Whole site | Commencement of construction | √ |
| S8.7 | S6.1 & 6.3 | Monthly audits of the waste management practices will be carried out during the construction phases to determine if wastes are being managed in accordance with the recommended good site practices. The audits will examine all aspects of waste management including waste generation, storage, recycling, transport and disposal. | Whole site | During construction | √ |

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Gammon Construction Ltd
- Δ Deficiency of Mitigation Measures but rectified by Gammon Construction Ltd
- N/A Not Applicable in Reporting Period

Annex H

Noise Monitoring Results

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results

NM6 Chancery Mansion

| Date | Start Time | End Time | Weather | Noise | level (dB(A) |), 30 min | Major Construction Noise Source(s) Observed | Other Noise Source(s) | Remarks | Wind Speed (m/s) | Noise Meter Model / ID | Calibrator Model / ID |
|-----------|------------|----------|---------|-------|--------------|-----------|--|--------------------------|---------|---------------------|---------------------------|--------------------------|
| | | | | Leq | L10 | L90 | | Observed | | (, | | |
| 06-Nov-17 | 9:12 | 9:42 | Sunny | 67.4 | 69.7 | 64.3 | Interior fitting (within the project site) | Traffic Noise | - | 0.4 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 10-Nov-17 | 9:30 | 10:00 | Sunny | 63.8 | 65.5 | 61.7 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 16-Nov-17 | 14:45 | 15:15 | Sunny | 64.5 | 66.2 | 62.6 | Interior fitting (within the project site) | Traffic Noise | - | 0.2 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 22-Nov-17 | 14:40 | 15:10 | Fine | 59.6 | 61.0 | 58.2 | Interior fitting (within the project site) | Traffic Noise | - | 0.8 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 28-Nov-17 | 13:05 | 13:35 | Cloudy | 65.4 | 67.2 | 63.1 | Interior fitting (within the project site) | Traffic Noise | - | 0.4 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| | Min. | | | | | | <u> </u> | | | | | |

Max. 67.4

NM2 Ho Fook Building

| | | | | Noise | level (dB(A) |), 30 min | Major Construction Noise | Other Noise | | Wind Speed | Noise Meter | Calibrator |
|-----------|------------|----------|---------|-------|--------------|-----------|--|-----------------------|---------|------------|---------------------------|--------------------------|
| Date | Start Time | End Time | Weather | Leq | L10 | L90 | Source(s) Observed | Source(s) Observed | Remarks | (m/s) | Model / ID | Model / ID |
| 06-Nov-17 | 9:50 | 10:20 | Sunny | 65.1 | 67.0 | 63.0 | Interior fitting (within the project site) | Traffic noise | - | 0.4 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 10-Nov-17 | 10:08 | 10:38 | Sunny | 65.6 | 67.1 | 62.4 | Interior fitting (within the project site) | Traffic Noise | - | 1.0 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 16-Nov-17 | 14:05 | 14:35 | Sunny | 65.9 | 67.3 | 63.0 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 22-Nov-17 | 14:00 | 14:30 | Fine | 67.3 | 71.3 | 62.4 | Interior fitting (within the project site) | Traffic Noise | - | 0.8 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 28-Nov-17 | 13:50 | 14:20 | Cloudy | 69.8 | 72.2 | 66.2 | Interior fitting (within the project site) | Traffic Noise | - | 0.4 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| | | | Min. | 65.1 | | | | | | | | |
| | | | Max. | 69.8 | | | | | | | | |

Note:
(a) Due to access issue, noise monitoring was conducted on the ground floor of NM6 on 22 November 2017.

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results

NM6 Chancery Mansion

| Date | Start Time | End Time | Weather | Noise | level (dB(A) |), 30 min | Major Construction Noise Source(s) Observed | Other Noise Source(s) | Remarks | Wind Speed (m/s) | Noise Meter Model / ID | Calibrator Model / ID |
|-----------|------------|----------|---------|-------|--------------|-----------|--|--------------------------|---------|---------------------|---------------------------|--------------------------|
| | | | | Leq | L10 | L90 | | Observed | | (| model/ is | |
| 04-Dec-17 | 10:42 | 11:12 | Sunny | 63.7 | 65.2 | 61.8 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 08-Dec-17 | 14:00 | 14:30 | Sunny | 63.9 | 65.4 | 61.5 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 14-Dec-17 | 9:23 | 9:53 | Fine | 66.9 | 69.2 | 63.4 | Interior fitting (within the project site) | Traffic Noise | - | 0.3 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 20-Dec-17 | 13:10 | 13:40 | Sunny | 73.8 | 76.8 | 67.1 | Breaking works, Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 23-Dec-17 | 8:30 | 9:00 | Sunny | 66.9 | 69.7 | 63.8 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 29-Dec-17 | 10:40 | 11:10 | Sunny | 66.6 | 68.4 | 63.9 | Interior fitting (within the project site) | Traffic Noise | - | 0.3 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| | | | Min. | 63.7 | | | | | | | | |

Min. 63.7 Max. 73.8

NM2 Ho Fook Building

| | | | | Noise | level (dB(A) |), 30 min | Major Construction Noise | Other Noise | | Wind Speed | Noise Meter | Calibrator |
|-----------|------------|----------|---------|-------|--------------|-----------|--|-----------------------|---------|------------|---------------------------|--------------------------|
| Date | Start Time | End Time | Weather | Leq | L10 | L90 | Source(s) Observed | Source(s) Observed | Remarks | (m/s) | Model / ID | Model / ID |
| 04-Dec-17 | 16:02 | 16:32 | Sunny | 66.7 | 68.9 | 62.9 | Interior fitting (within the project site) | Traffic noise | - | 0.4 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 08-Dec-17 | 9:50 | 10:20 | Sunny | 68.1 | 70.5 | 64.5 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 14-Dec-17 | 10:00 | 10:30 | Fine | 66.3 | 67.9 | 63.3 | Interior fitting (within the project site) | Traffic Noise | - | 0.3 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 20-Dec-17 | 13:50 | 14:20 | Sunny | 68.4 | 70.9 | 62.7 | Interior fitting (within the project site) | Traffic Noise | - | 0.2 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 23-Dec-17 | 9:07 | 9:37 | Sunny | 66.9 | 68.6 | 63.3 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 29-Dec-17 | 10:00 | 10:30 | Sunny | 69.0 | 70.7 | 65.5 | Interior fitting (within the project site) | Traffic Noise | - | 0.3 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| | | | Min. | 66.3 | | | | | | | | • |
| | | | | 000 | | | | | | | | |

Min. 66.3 Max. 69.0

Annex H Noise Monitoring Results

Daytime Noise Monitoring Results


NM6 Chancery Mansion


| Date | Start Time | End Time | Weather | Noise | level (dB(A) |), 30 min | Major Construction Noise Source(s) Observed | Other Noise Source(s) | Remarks | Wind Speed (m/s) | Noise Meter Model / ID | Calibrator Model / ID |
|-----------|------------|----------|---------|-------|--------------|-----------|--|--------------------------|---------|---------------------|---------------------------|--------------------------|
| | | | | Leq | L10 | L90 | 554.55(5) 5255.754 | Observed | | (-1) | | |
| 04-Jan-18 | 8:30 | 9:00 | Fine | 66.2 | 67.8 | 63.6 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 10-Jan-18 | 9:55 | 10:25 | Cloudy | 65.2 | 66.9 | 63.1 | Interior fitting (within the project site) | Traffic Noise | - | 1.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 16-Jan-18 | 13:10 | 13:40 | Sunny | 64.4 | 66.1 | 61.8 | Interior fitting (within the project site) | Traffic Noise | - | 0.4 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 22-Jan-18 | 8:45 | 9:15 | Sunny | 65.7 | 67.4 | 63.0 | Breaking works, Interior fitting (within the project site) | Traffic Noise | - | 0.4 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 26-Jan-18 | 9:42 | 10:12 | Sunny | 64.9 | 66.7 | 62.7 | Interior fitting (within the project site) | Traffic Noise | - | 0.6 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| | | | Min. | 64.4 | | | | | | | | |
| | | | Max. | 66.2 | | | | | | | | |

NM2 Ho Fook Building

| | | | | Noise | level (dB(A) |), 30 min | Major Construction Noise | Other Noise | | Wind Speed | Noise Meter | Calibrator |
|-----------|------------|----------|---------|-------|--------------|-----------|--|-----------------------|---------|------------|---------------------------|--------------------------|
| Date | Start Time | End Time | Weather | Leq | L10 | L90 | Source(s) Observed | Source(s) Observed | Remarks | (m/s) | Model / ID | Model / ID |
| 04-Jan-18 | 10:25 | 10:55 | Fine | 69.9 | 72.3 | 66.1 | Interior fitting (within the project site) | Traffic noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 10-Jan-18 | 10:34 | 11:04 | Cloudy | 68.4 | 71.1 | 64.5 | Interior fitting (within the project site) | Traffic Noise | - | 1.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 16-Jan-18 | 13:50 | 14:20 | Sunny | 68.4 | 71.1 | 64.0 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 22-Jan-18 | 9:24 | 9:54 | Sunny | 69.3 | 71.7 | 64.8 | Interior fitting (within the project site) | Traffic Noise | - | 0.5 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| 26-Jan-18 | 10:22 | 10:52 | Sunny | 68.1 | 70.8 | 64.8 | Interior fitting (within the project site) | Traffic Noise | - | 1.0 | CEL-633A (S/N 3521757) | CEL-120 (S/N 3421612) |
| | | | Min. | 68.1 | | | | | | | | |


Min. 68.1 Max. 69.9

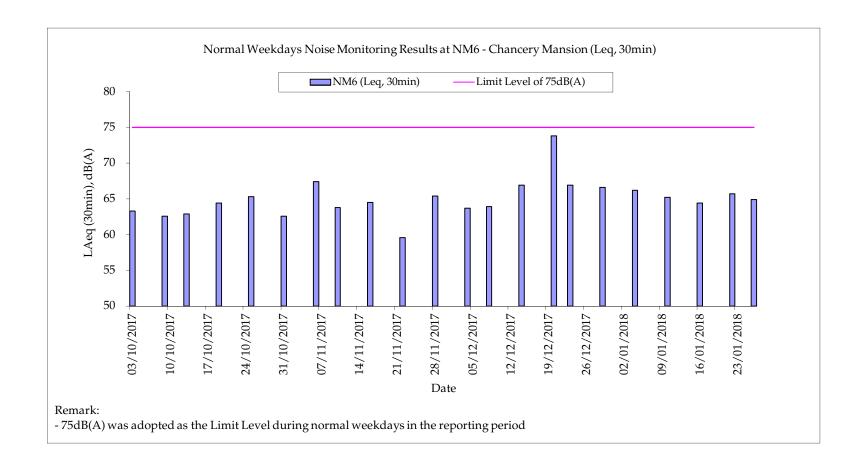


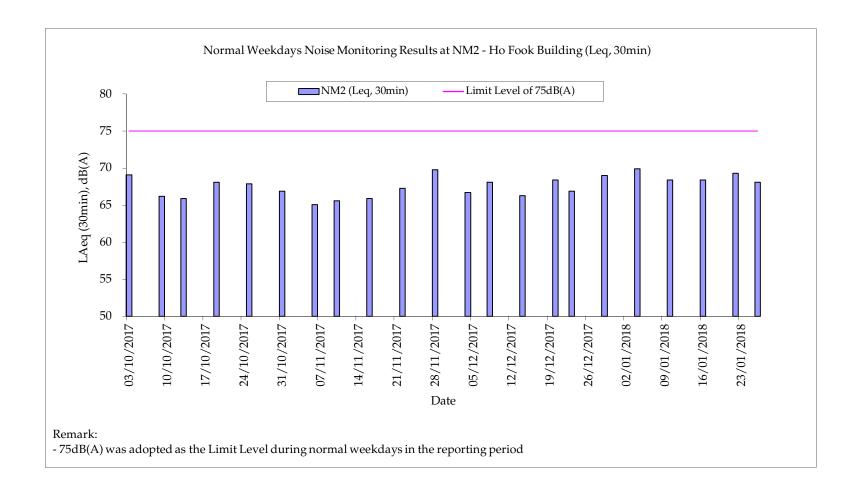


Annex I

Construction Programme for the Project

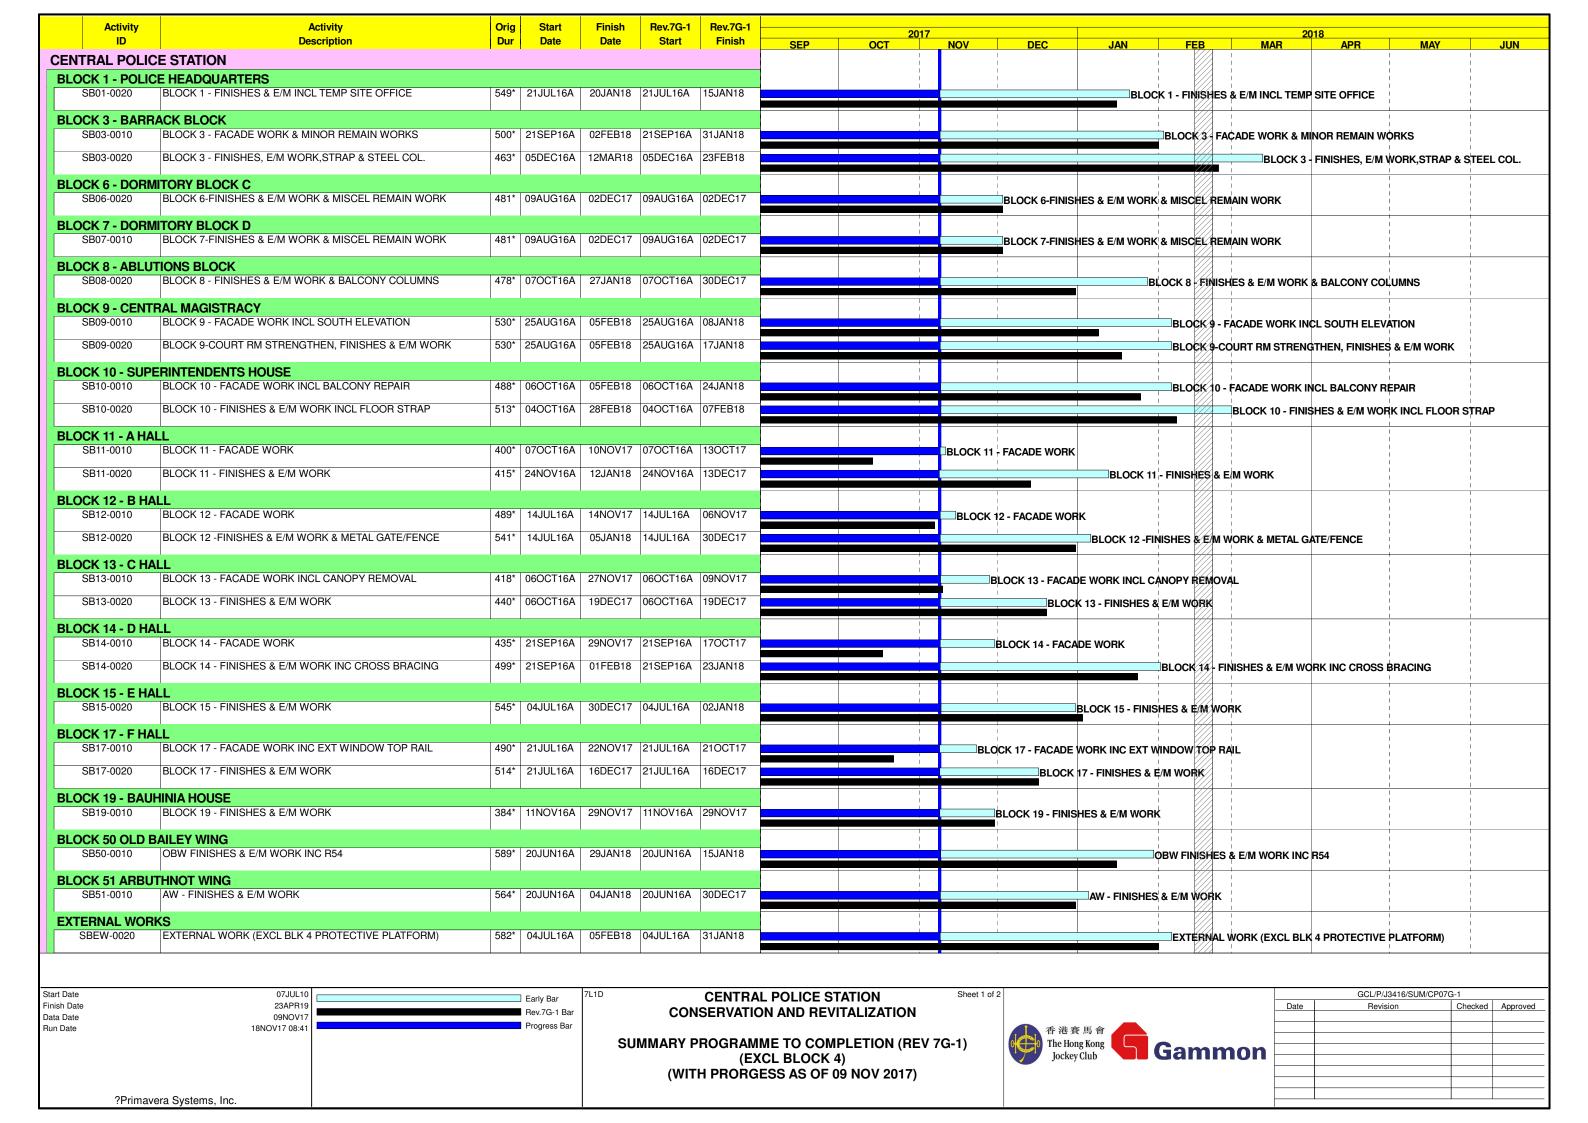

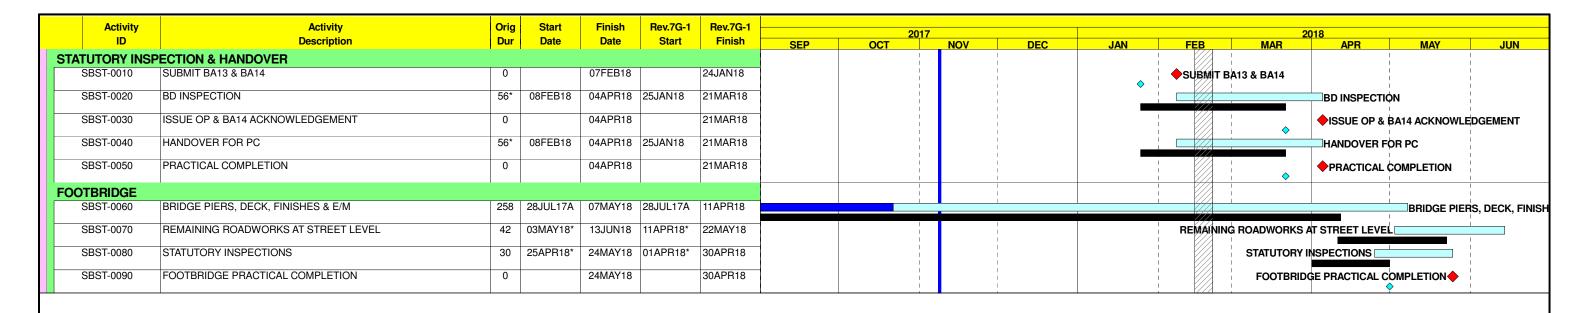





CENTRAL POLICE STATION
CONSERVATION AND REVITALIZATION

SUMMARY PROGRAMME TO COMPLETION (REV 7G-1) (EXCL BLOCK 4) (WITH PRORGESS AS OF 09 NOV 2017)



| | GCL/P/J3416/SUM/CPU/C | ו-ג | |
|------|-----------------------|---------|----------|
| Date | Revision | Checked | Approved |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | • | |

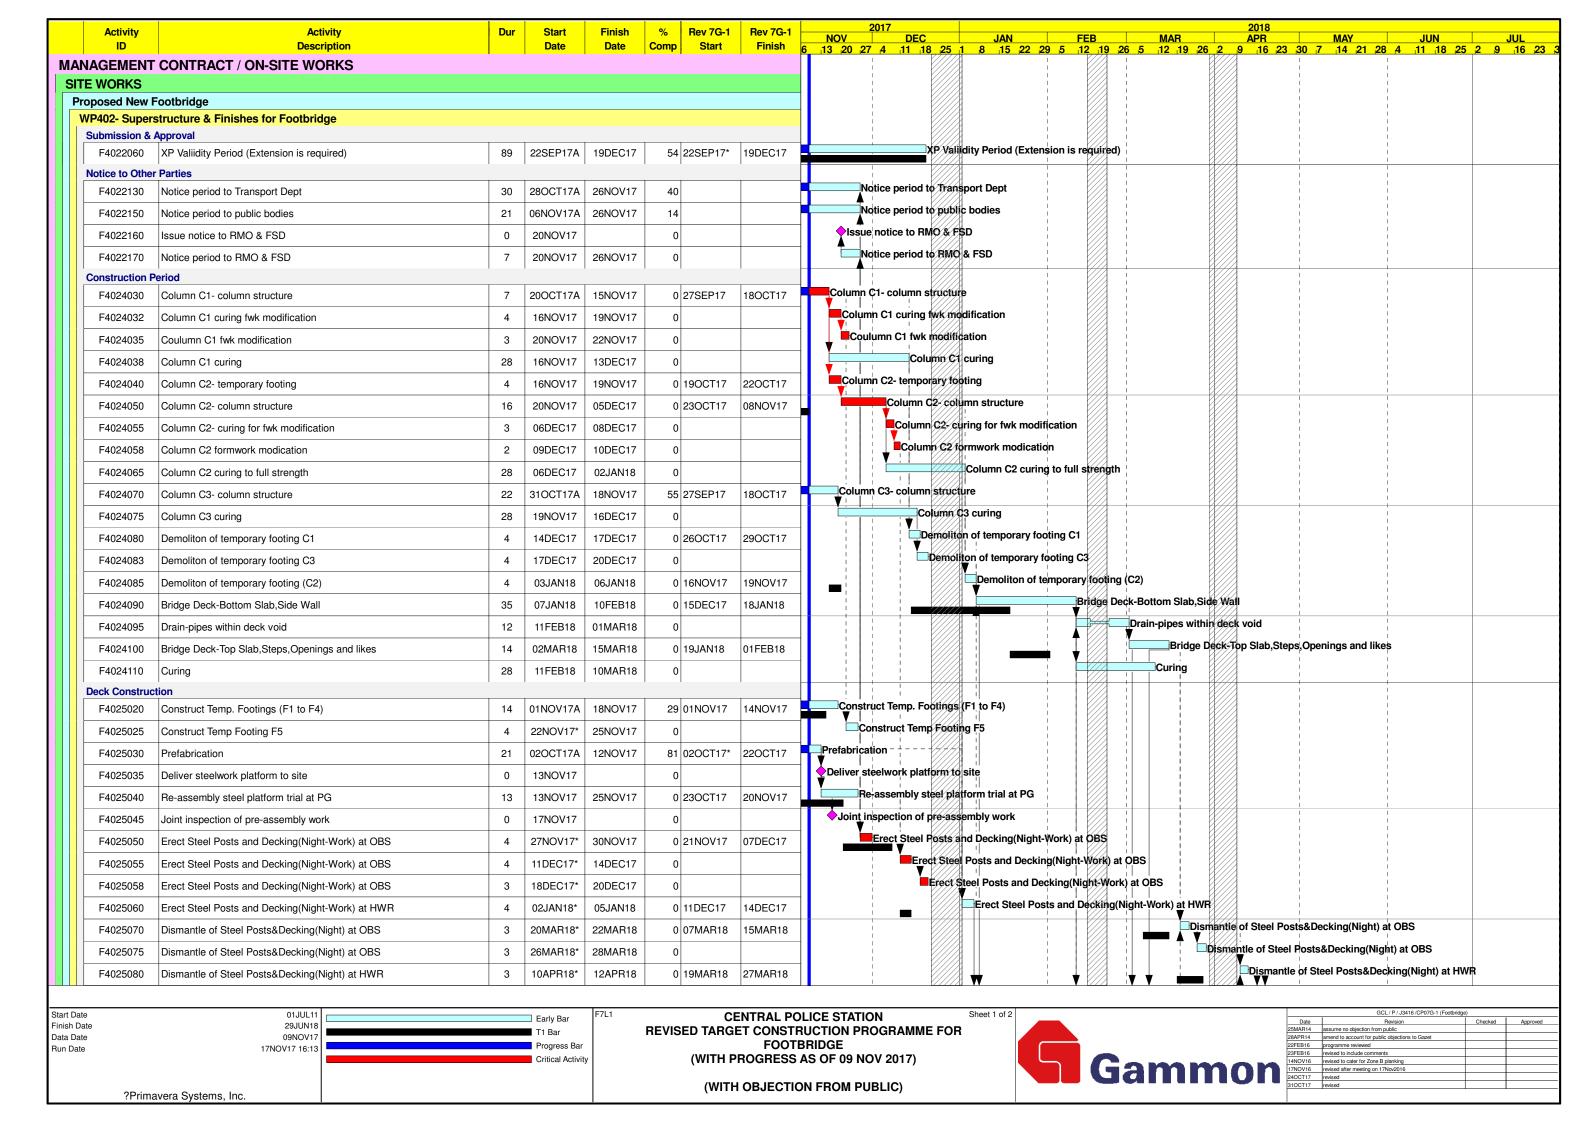

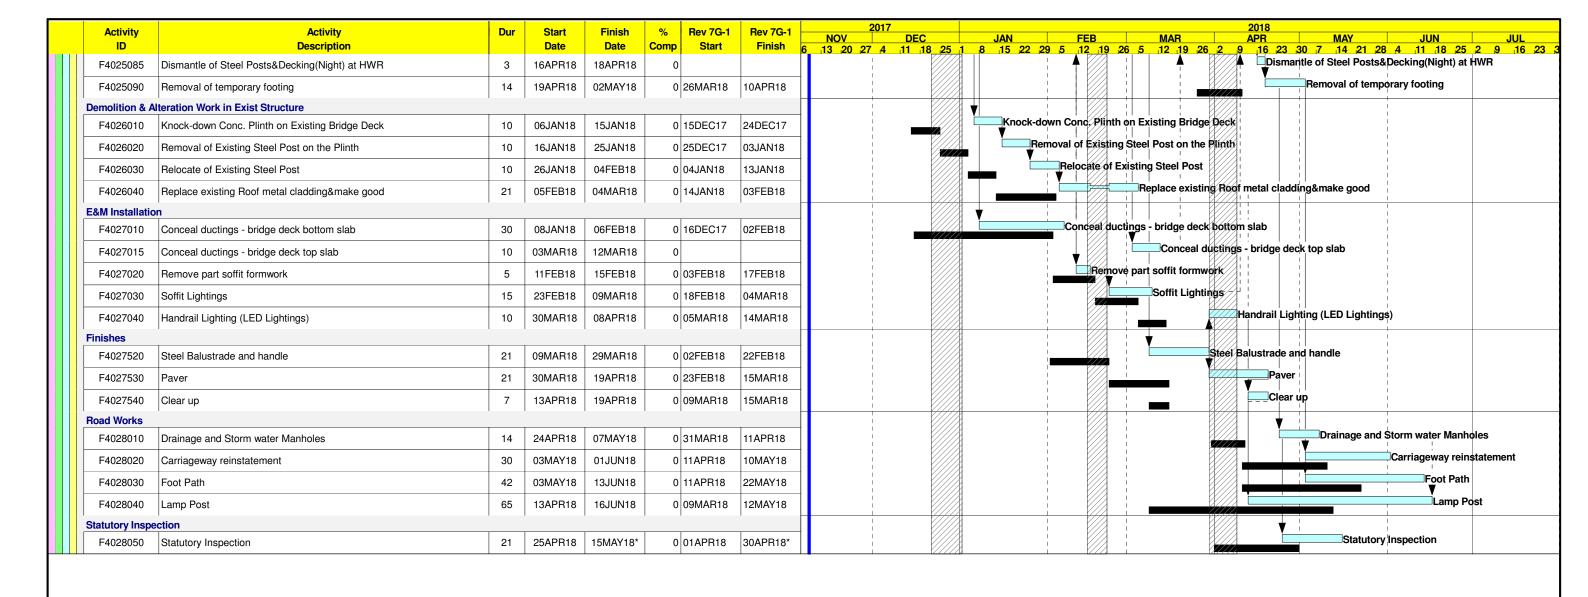

 Start Date
 01JUL11

 Finish Date
 29JUN18

 Data Date
 09NOV17

 Run Date
 17NOV17 16:13

 Early Bar

 T1 Bar

 Progress Bar

 Critical Activity

?Primavera Systems, Inc.

CENTRAL POLICE STATION
REVISED TARGET CONSTRUCTION PROGRAMME FOR
FOOTBRIDGE
(WITH PROGRESS AS OF 09 NOV 2017)

(WITH OBJECTION FROM PUBLIC)



| | GCL / P / J3416 /CP07G-1 (Footb | oridge) | |
|---------|---|-----------------------------|----------|
| Date | Revision | Checked | Approved |
| 25MAR14 | assume no objection from public | | |
| 28APR14 | amend to account for public objections to Gazet | | |
| 22FEB16 | programme reviewed | programme reviewed | |
| 23FEB16 | revised to include comments | revised to include comments | |
| 14NOV16 | revised to cater for Zone B planking | | |
| 17NOV16 | revised after meeting on 17Nov2016 | | |
| 24OCT17 | revised | | |
| 31OCT17 | revised | | - |

Annex J

Waste Flow Table

Annex J – Waste Flow Table

| Month / Year | Canada | No | V-1 | CODM | | antity | Ch | Chemical Recycled materials | | | |
|----------------------|---------------------------------------|---|---|------------------|---|--|------|-----------------------------|----------------------|---------------|--------------|
| | C&D Materials (inert) (tonnes) (a) | Number of Trucks for C&D Materials Disposal (inert) | Volume of C&D Materials (inert) (m ³) (c) | | Number of Trucks for C&D Materials Disposal (non-inert) | Volume of C&D Materials (non- inert) (m ³) (c) | | Waste (Liquid/L) | Recycled materials | Plastics (kg) | Matala flor |
| | | - | | | | | _ | - | Paper/cardboard (kg) | riastics (kg) | Metals (kg |
| ctober 2011 – | | | | | | | | | | | |
| ovember 2011 | 0 | 0 | 0 | 33.5 | 12 | 58.50 | 0 | 0 | 38 | 6 | 36423 |
| ecember-11 | 0 | 0 | 0 | 18.25 | 6 | 29.25 | 0 | 0 | 112 | 0 | 24000 |
| nuary-12 | 354.14 | 40 | 195.00 | 16.88 | 5 | 24.38 | 2400 | 0 | 0 | 0 | 3820 |
| bruary-12 | 252.35 | 15 | 73.13 | 17.13 | 5 | 24.38 | 1400 | 0 | 223 | 0 | 8910 |
| arch-12 | 666.43 | 62 | 302.25 | 28.56 | 9 | 43.88 | 3200 | 0 | 0 | 0 | 4849 |
| pril-12 | 688.68 | 72 | 351.00 | 17.54 | 5 | 24.38 | 0 | 0 | 0 | 0 | 12403 |
| ay-12 | 492.33 | 61 | 297.38 | 36.33 | 13 | 63.38 | 0 | 0 | 266 | 0 | 0 |
| ne-12 | 383.11 | 45 | 219.38 | 27.41 | 8 | 39.00 | 40 | 45 | 0 | 0 | 1100 |
| ly-12 | 217.98 | 25 | 121.88 | 23.22 | 8 | 39.00 | 0 | 0 | 302 | 0 | 1750 |
| ugust-12 | 341.87 | 42 | 204.75 | 48.87 | 16 | 78.00 | 0 | 0 | 0 | 0 | 2310 |
| ptember-12 | 227.7 | 29 | 141.38 | 37.99 | 12 | 58.50 | 0 | 0 | 383 | 0 | 1410 |
| tober-12 | 290.58 | 44 | 214.50 | 30.34 | 8 | 39.00 | 0 | 0 | 86 | 0 | 3150 |
| ovember-12 | 843.86 | 100 | 487.50 | 47.44 | 15 | 73.13 | 0 | 0 | 0 | 0 | 5650 |
| ecember-12 | 207.5 | 27 | 131.63 | 88.66 | 28 | 136.50 | 0 | 0 | 0 | 0 | 2723 |
| nuary-13 | 273.64 | 34 | 165.75 | 276.17 | 74 | 360.75 | 0 | 0 | 172 | 0 | 8120 |
| bruary-13 | 945.97 | 131 | 638.63 | 177.54 | 46 | 224.25 | 0 | 0 | 0 | 0 | 1080 |
| arch-13 | 1236.96 | 151 | 736.13 | 230.55 | 60 | 292.50 | 0 | 0 | 164 | 0 | 11300 |
| pril-13 | 1406.79 | 187 | 911.63 | 232.27 | 63 | 307.13 | 135 | 12 | 225 | 0 | 21220 |
| ay-13 | 2679.91 | 317 | 1545.38 | 176.68 | 44 | 214.50 | 0 | 0 | 62 | 0 | 17286 |
| ne-13 | 3062.38 | 356 | 1735.50 | 212.63 | 56 | 273.00 | 0 | 0 | 0 | 0 | 7150 |
| ly-13 | 3814.86 | 465 | 2266.88 | 114.36 | 43 | 209.63 | 0 | 0 | 168 | 0 | 1484 |
| ugust-13 | 2831.78 | 353 | 1720.88 | 89.23 | 25 | 121.88 | 0 | 0 | 0 | 0 | 7190 |
| ptember-13 | 979.49 | 141 | 687.38 | 103.73 | 29 | 141.38 | 40 | 0 | 0 | 0 | 4030 |
| ctober-13 | 2170.54 | 270 | 1316.25 | 157.48 | 41 | 199.88 | 135 | 0 | 0 | 0 | 3120 |
| ovember-13 | 836.74 | 109 | 531.38 | 191.58 | 44 | 214.50 | 0 | 0 | 202 | 0 | 1848 |
| ecember-13 | 2606.76 | 296 | 1443.00 | 192.54 | 49 | 238.88 | 0 | 0 | 0 | 0 | 1004 |
| nuary-14 | 3813.53 | 400 | 1950.00 | 97.87 | 36 | 175.50 | 0 | 0 | 0 | 0 | 14110 |
| bruary-14 | 3378.16 | 316 | 1540.50 | 37.84 | 14 | 68.25 | 0 | 0 | 0 | 0 | 9800 |
| arch-14 | 5256.15 | 516 | 2515.50 | 89.39 | 31 | 151.13 | 0 | 0 | 6000 | 0 | 1903 |
| pril-14 | 3006 | 299 | 1457.63 | 114.31 | 33 | 160.88 | 45 | 0 | 0 | 0 | 6950 |
| ay-14 | 3195.53 | 310 | 1511.25 | 119.54 | 37 | 180.38 | 0 | 0 | 0 | 0 | 7000 |
| ne-14 | 2176.81 | 205 | 999.38 | 148.8 | 45 | 219.38 | 0 | 0 | 242 | 0 | 8830 |
| ly-14 | 1009.96 | 111 | 541.13 | 147.36 | 49 | 238.88 | 0 | 0 | 0 | 0 | 6680 |
| ugust-14 | 379.23 | 53 | 258.38 | 211.86 | 47 | 229.13 | 0 | 0 | 0 | 0 | 1369 |
| ptember-14 | 1216.97 | 123 | 599.63 | 264.83 | 56 | 273.00 | 0 | 0 | 0 | 0 | 9720 |
| ctober-14 | 1162.34 | 124 | 604.50 | 294.33 | 65 | 316.88 | 0 | 0 | 0 | 0 | 5708 |
| ovember-14 | 1249.55 | 141 | 687.38 | 336.57 | 75 | 365.63 | 0 | 0 | 0 | 0 | 6660 |
| ecember-14 | 1177.63 | 129 | 628.88 | 260.33 | 69 | 336.38 | 0 | 0 | 68 | 0 | 1208 |
| nuary-15 | 614.34 | 69 | 336.38 | 222.32 | 58 | 282.75 | 0 | 0 | 0 | 0 | 3000 |
| bruary-15 | 593.97 | 78 | 380.25 | 133.74 | 40 | 195.00 | 0 | 0 | 0 | 0 | 5420 |
| arch-15 | 766.35 594.77 | 93 78 | 453.38 380.25 | 245.77 195.55 | 71 51 | 346.13 248.63 | 0 | 0 | 106 0 | 0 | 8980 3370 |
| pril-15 | | | | | | | | | | 0 | |
| ay-15 | 832.50 | 110 | 536.25 | 212.04 | 63 72 | 307.13 | 0 | 0 | 133 23 | 0 | 5090 |
| ne-15 | 673.87 | 84 | 409.50 | 222.66 | | 351.00 | 0 | 0 | | 0 | 0 |
| ly-15 | 1133.90 1394.20 | 137 157 | 667.88 765.38 | 184.02 226.04 | 62 | 302.25 394.88 | 0 | 0 | 0 | 0 | 6950 |
| ugust-15 | | | | | 81 | | | | 0 | 0 | 0 |
| ptember-15 | 942.39 1874.26 | 107 220 | 521.63 1072.50 | 330.23 286.27 | 108 109 | 526.50 531.38 | 0 | 0 | 0 60 | 0 | 0 |
| ctober-15 | | | | | | | | | | 0 | |
| ovember-15 | 830.67 596.00 | 93 58 | 453.38 282.75 | 321.6 250.51 | 117 107 | 570.38 521.63 | 0 | 0 | 86 103 | 0 | 4970 1677 |
| ecember-15 | | | | | | | | | | 0 | |
| nuary-16 | 505.11 274.16 | 57 30 | 277.88 146.25 | 265.56 128.66 | 120 70 | 585.00 341.25 | 0 | 0 | 0 170 | 0 | 6340 0 |
| bruary-16 arch-16 | 274.16 114.67 | 30 17 | 146.25 82.88 | 128.66 380.06 | 70 116 | 341.25 565.50 | 0 | 0 | 170 0 | 0 | 0 |
| | 114.67 244.83 | 17 34 | 82.88 165.75 | 380.06 308.28 | 116 113 | 565.50 550.88 | 0 | 0 | | | 0 |
| pril-16 | 402.49 | 55 | 268.13 | 308.28 216.79 | 74 | 360.75 | 0 | 0 | 0 | 0 | 0 |
| ay-16 | 402.49 173.01 | 55 20 | 268.13 97.50 | 216.79 109.25 | 74 36 | 360.75 175.50 | 0 | 0 | 0 248 | | 0 |
| ne-16 | 173.01 303.68 | 20 37 | 97.50 180.38 | 109.25 83.99 | 36 40 | 175.50 195.00 | 0 | 0 | 248 0 | 0 | |
| ly-16 | 303.68 147.28 | 37 19 | 180.38 92.63 | 83.99 112.63 | 40 46 | 195.00 224.25 | 0 | 0 | | 0 | 0 |
| ugust-16 | | 19 3 | | | 46 39 | | 0 | | 0 226 | 0 | |
| ptember-16 | 17.64 | | 14.63 | 88.26 | | 190.13 | | 0 | | 0 | 0 |
| tober-16 | 57.59 | 9 | 43.88 | 69.64 | 28 | 136.50 | 0 | 0 | 0 | 0 | 0 |
| vember-16 | 14.21 | 2 | 9.75 | 105.39 | 33 | 160.88 | 0 | 0 | 0 | 0 | 0 |
| cember-16 | 29.61 | 4 | 19.50 | 69.45 | 27 | 131.63 | 0 | 0 | 260 | 0 | 0 |
| uary-17 | 27.51 | 4 | 19.50 | 51.97 | 22 | 107.25 | 0 | 0 | 190 | 0 | 0 |
| oruary-17 | 60.97 | 9 | 43.88 | 43.89 | 15 | 73.13 | 0 | 0 | 210 | 0 | 0 |
| rch-17 | 135.47 | 17 | 82.88 | 93.05 | 27 | 131.63 | 0 | 0 | 160 | 0 | 0 |
| ril-17 | 32.19 | 4 | 19.50 | 103.21 | 28 | 136.50 | 0 | 0 | 0 | 0 | 0 |
| ny-17 | 54.34 | 8 | 39.00 | 87.19 | 26 | 126.75 | 0 | 0 | 228 | 0 | 0 |
| ne-17 | 134.59 | 15 | 73.13 | 80.65 | 30 | 146.25 | 0 | 0 | 266 | 0 | 0 |
| y-17 | 12.61 | 1 | 4.88 | 57.54 | 24 | 117.00 | 0 | 0 | 0 | 0 | 0 |
| gust-17 | 79.39 | 10 | 48.75 | 58.03 | 24 | 117.00 | 0 | 0 | 0 | 0 | 0 |
| otember-17 | 199.78 | 24 | 117.00 | 62.43 | 25 | 121.88 | 0 | 0 | 382 | 0 | 0 |
| tober-17 | 103.07 | 12 | 58.50 | 50.09 | 24 | 117.00 | 0 | 0 | 0 | 0 | 0 |
| vember-17 | 92.76 | 13 | 63.38 | 129.3 | 40 | 195.00 | 0 | 0 | 270 | 0 | 0 |
| cember-17 | 86.17 | 13 | 63.38 | 106.77 | 35 | 170.63 | 0 | 0 | 1612 | 0 | 0 |
| nuary-18 | 87.24 | 13 | 63.38 | 186.5 | 66 | 321.75 | 0 | 0 | 0 | 0 | 0 |
| | al 69071.8 | 7813 | 38088.38 | 10629.24 | 3348 | 16321.50 | 7395 | 57 | 13446 | 6 | 6446 |

Notes:

(a) Inert C&D materials (public fill) include bricks, concrete, building debris, rubble and excavated soil.

⁽b) Non-inert C&D materials include wastes such as general refuse and mixed construction waste.

⁽c) If necessary, use the conversion factor: 3/4 load of dumping truck being equivalent to $6.5~\mathrm{m}^3$ by volume.

⁽d) 382 kg, 270 kg and 1612 kg of paper/cardboard packaging were recycled in September, November and December 2017, respectively. The quantities were reported by Contractor after the submission of the aforementioned monthly EM&A reports.

Annex K

Environmental Complaint, Environmental Summons and Prosecution Log

Annex K Cumulative Complaint and Summons/Prosecutions Log

| Reporting Month | Number of Complaints in Reporting Month | Number of Summons/Prosecutions in Reporting Month |
|-----------------|---|---|
| November 2011 | 0 | 0 |
| December 2011 | 0 | 0 |
| January 2012 | 0 | 0 |
| February 2012 | 0 | 0 |
| March 2012 | 4 | 0 |
| April 2012 | 0 | 0 |
| May 2012 | 0 | 0 |
| June 2012 | 2 | 0 |
| July 2012 | 1 | 0 |
| August 2012 | 0 | 0 |
| September 2012 | 0 | 0 |
| October 2012 | 0 | 0 |
| November 2012 | 2 | 0 |
| December 2012 | 0 | 0 |
| January 2013 | 0 | 0 |
| February 2013 | 1 | 0 |
| March 2013 | 1 | 0 |
| April 2013 | 0 | 0 |

| Reporting Month | Number of Complaints in Reporting Month | Number of Summons/Prosecutions in Reporting Month |
|-----------------|---|---|
| May 2013 | 0 | 0 |
| June 2013 | 0 | 0 |
| July 2013 | 0 | 0 |
| August 2013 | 0 | 0 |
| September 2013 | 0 | 0 |
| October 2013 | 0 | 0 |
| November 2013 | 0 | 0 |
| December 2013 | 0 | 0 |
| January 2014 | 2 | 0 |
| February 2014 | 1 | 0 |
| March 2014 | 1 | 0 |
| April 2014 | 1 | 0 |
| May 2014 | 0 | 0 |
| June 2014 | 0 | 0 |
| July 2014 | 2 | 0 |
| August 2014 | 3 | 0 |
| September 2014 | 2 | 0 |
| October 2014 | 1 | 0 |
| November 2014 | 0 | 0 |

| Reporting Month | Number of Complaints in Reporting Month | Number of Summons/Prosecutions in Reporting Month |
|-----------------|---|---|
| December 2014 | 0 | 0 |
| January 2015 | 0 | 0 |
| February 2015 | 1 | 0 |
| March 2015 | 1 | 0 |
| April 2015 | 0 | 0 |
| May 2015 | 1 | 0 |
| June 2015 | 1 | 0 |
| July 2015 | 1 | 0 |
| August 2015 | 1 | 0 |
| September 2015 | 0 | 0 |
| October 2015 | 0 | 0 |
| November 2015 | 0 | 0 |
| December 2015 | 0 | 0 |
| January 2016 | 0 | 0 |
| February 2016 | 0 | 0 |
| March 2016 | 1 | 0 |
| April 2016 | 0 | 0 |
| May 2016 | 0 | 0 |
| June 2016 | 0 | 0 |

| Reporting Month | Number of Complaints in Reporting Month | Number of Summons/Prosecutions in Reporting Month |
|-----------------|---|---|
| July 2016 | 0 | 0 |
| August 2016 | 0 | 0 |
| September 2016 | 1 | 0 |
| October 2016 | 0 | 0 |
| November 2016 | 0 | 0 |
| December 2016 | 0 | 0 |
| January 2017 | 0 | 0 |
| February 2017 | 0 | 0 |
| March 2017 | 0 | 0 |
| April 2017 | 0 | 0 |
| May 2017 | 0 | 0 |
| June 2017 | 0 | 0 |
| July 2017 | 0 | 0 |
| August 2017 | 0 | 0 |
| September 2017 | 0 | 0 |
| October 2017 | 0 | 0 |
| November 2017 | 0 | 0 |
| December 2017 | 1 | 0 |
| January 2018 | 1 | 0 |

| Reporting Month | Number of Complaints in Reporting Month | Number of Summons/Prosecutions in Reporting Month |
|-----------------|---|---|
| Overall Total | 34 | 0 |









Central Police Station Conservation and Revitalisation Project



COMPLAINT INVESTIGATION REPORT

Basic Information of Complaint

| Log Number: | 2017/12/001 |
|----------------------------|---|
| Date of Complaint Received | 19 December 2017 |
| Location of Complaint | Project Site |
| Nature of Complaint | Noise nuisance |
| Complaint Received by | Environmental Protection Department (EPD) |
| Complainant | Management office of Chancery Lane 5B in the vicinity of CPS site |

Details of Complaint


A noise complaint was transferred by the EPD to the Environmental Team (ET) on 19 December 2017. The complainant complained about noise nuisance from ground breaking activities at the CPS site recently that have persisted for about 1 week. The mentioned noise commenced at around 08:00 hour and last until the afternoon every day. The complainant is requesting the implementation of noise mitigation measure to reduce the noise impact from the CPS site.

Investigation Report

- As advised by Gammon Construction Limited (the Contractor), breaking works for removal of concrete surface are currently being carried out near Block 14. The location of the concrete breaking works is shown in the figure below.
 The concrete breaking works, which are performed during working hours, are expected to be completed on or before 3 January 2018.
- 2. Weekly noise monitoring at the two designated noise monitoring locations (NM2 and NM6) is being carried out as part of the Environmental Monitoring and Audit (EM&A) requirements. Latest noise monitoring data on 4, 8, 14 and 20 December 2017 are presented below:

| Monitoring Date | Leq, 30minute (dB(A)) | | |
|--------------------------------|-----------------------|------|--|
| | NM2 | NM6 | |
| 4 December 2017 | 66.7 | 63.7 | |
| 8 December 2017 | 68.1 | 63.9 | |
| 14 December 2017 | 66.3 | 66.9 | |
| 20 December 2017 | 68.4 | 73.8 | |
| Leq, 30minute Noise Criterion: | 75 | 75 | |

It can be seen that recent noise measurements at NM2 and NM6 comply with the relevant noise criterion. Concrete breaking works were carried out during the noise monitoring period on 20 December 2017 and the measured noise level during that period complied with the noise criterion.

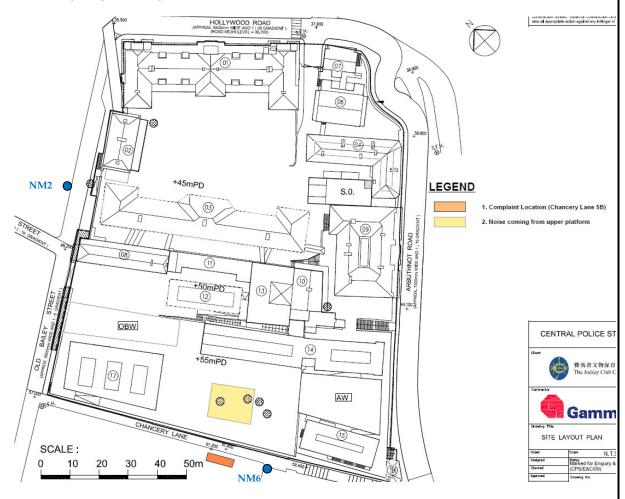

3. After receiving the complaint, the Contractor has provided acoustic blanket to the head of the breaker and such provision shall continue to be implemented when the breaker is used.

Mitigation Measures and Follow-up Actions Recommended to Contractor

All construction works are carried out strictly following the necessary requirements specified in EIA, EM&A Manual, EMP, Method Statements, General and Particular Specifications of this Project. The Contractor is recommended to provide acoustic blanket to the head of the breaker during the concrete breaking works to reduce the noise generated. As advised by the Contractor, the concrete breaking works is expected to last until 3 January 2018. As a general reminder, the concrete breaking works are only permitted during normal working hours, i.e. between 7am and 7pm on normal working days without a valid Construction Noise Permit (CNP). The Contractor should also carry out other work activities with care to avoid causing unnecessary noise nuisance as much as possible.

Date of File Closed:

21 December 2017

Approved by:

ET Leader

IEC

JCCPS's

Representative

Rocco Design Architect's

Representative

(Name: Katie Yu)

Date: 21 December 2017

(Name: Keith Chau)

Date: 22 December 2017

(Name: CW Sham)

(Name: Kung

Date: 22 December 2017 Date: 22 DEC 2017

Gammon's Representative

(Name: O

20:7-12-22











Central Police Station Conservation and Revitalisation Project

COMPLAINT INVESTIGATION REPORT

Basic Information of Complaint

| Log Number: | 2018/02/001 |
|----------------------------|---|
| Date of Complaint Received | 2 February 2018 |
| Location of Complaint | Project Site |
| Nature of Complaint | Construction waste |
| Complaint Received by | Environmental Protection Department (EPD) |
| Complainant | |

Details of Complaint

A complaint on improper storage of construction waste was received by the EPD on 29 January 2018 and transferred to the Environmental Team (ET) on 2 February 2018. The complainant complained that illegal dumping of construction waste was observed at Old Bailey Street and at the junction of Old Bailey Street and Hollywood Road, causing hygiene problem as well as obstruction of the road. The complainant did not specifically complain about the ongoing footbridge construction of the CPS Project.

Investigation Report

- 1. As advised by Gammon Construction Limited (the Contractor), one waste skip belonging to the CPS Site is located near the main entrance gate (blue gate) on the sidewalk of Old Bailey Street. The waste skip is located within the barricaded area on the east sidewalk of Old Bailey Street which is part of the approved road works area for CPS. The waste skip would not cause obstruction to road or pedestrians. A photo of the waste skip is shown in *Photo 1* and its location is shown in *Figure 1*. Construction waste generated from the CPS Site would be temporarily deposited in the waste skip, which will be cleared at the end of each working day. There is no illegal dumping of construction waste from the CPS Site. It should be noted that this waste skip has been in the same location for at least the past 1-2 years.
- 2. A small area at the junction of Old Bailey Street and Hollywood was barricaded for temporary storage of materials for the ongoing footbridge construction. A photo of the temporary storage area is shown in *Photo* 2 and its location is shown in *Figure* 1. No construction waste is placed in the temporary storage area. The temporary storage area, which is included in the approved works area for the footbridge construction, only occupies part of the sidewalk of Hollywood Road and is considered not causing significant obstruction to the pedestrians. The temporary storage area would be in place until June 2018 which is the expected completion month of the footbridge construction.
- 3. A waste skip which belongs to a construction site opposite to the CPS Site is located on the west side of Old Bailey Street near the junction of Old Bailey Street and Hollywood (*Figure 1*). A photo of the waste skip is shown in *Photo 3*. As the complainant mentioned the presence of the waste skip causing obstruction of road at Old Bailey Street, it is suspected that the complainant is referring to this waste skip which is not managed by the CPS Site.






Photo 1: Construction Waste Skip (CPS Site)

Photo 2: Temporary Storage Area (CPS Site)



Photo 3: Construction Waste Skip (Other Construction Site)

Figure 1 - Locations of Construction Waste Skips and Temporary Storage Area

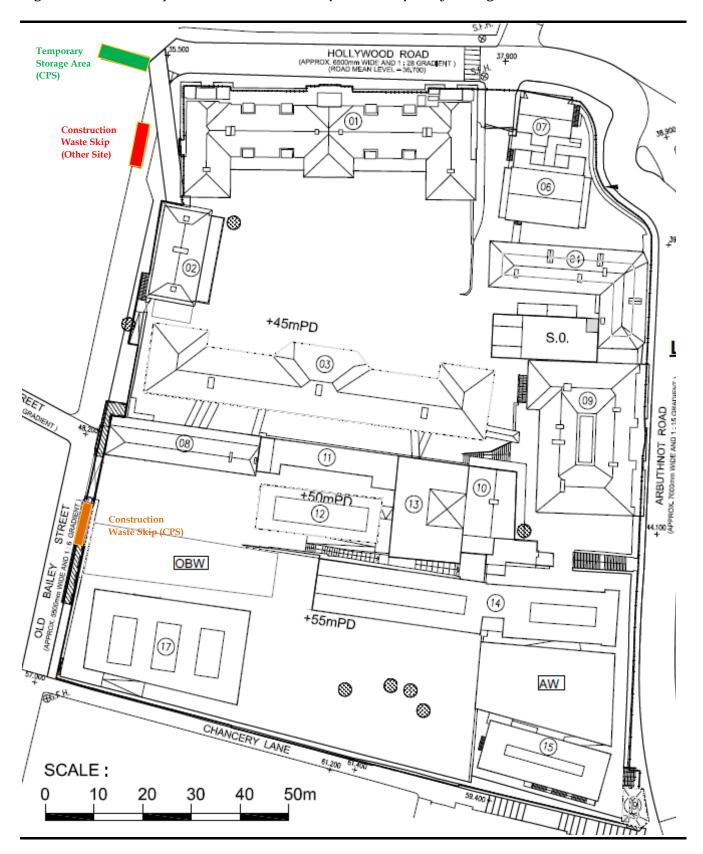

Mitigation Measures and Follow-up Actions Recommended to Contractor

All construction works are carried out strictly following the necessary requirements specified in EIA, EM&A Manual, EMP, Method Statements, General and Particular Specifications of this Project. The Contractor has been reminded to maintain tidiness of the construction waste skip and its surroundings. Construction waste should only be stored inside the waste skip and should be cleared on a daily basis to prevent accumulation. With regard to the temporary storage area at the junction of Old Bailey Street and Hollywood Road, the Contractor was also reminded to keep the temporary storage area tidy and clear of litter.

Date of File Closed:

12 February 2018

Approved by:

ET Leader

IEC

JCCPS's

Representative

Rocco Design Architect's

Representative

(Name: Katie Yu)

Date: 12 February 2018

(Name: Keith Chau) Date: 15-Feb-2018

(Name:

Date: 21 Feb 20/8 Date: 21 FEB 2018

Gammon's Representative

(Name: CLIFF LEVING

Date:

2018-02-15

Annex L

Records of Vibration Monitoring for Other Construction Works

Structural Additions and Alterations at Block 11 WYNDHAM \$ STREET 22-3/3066/10/BLK11 (HU) (S) F.S.D. Ref No. 消防療機築編號 11SW-B/R18 11SW-B/R17 Shiu King The Centrium Gourt - 11SW-B/R806 11SW-B/R23-11SW-B/R52 GS12 - 11SW-B/R24 BS14-17 CHIONG Kam-yueng lacky Chief Structural Engineer for BUILDING AUTHORITY BS13-3 - 3 OCT 2612 ₩15-2 11SW-B/R53 11SW-B/R176 **Д**VM15−1 BS3-5/ BT3-3 11SW-B/R19 BS1-14/ BT1-7 11SW-8/R174 ₩BS14-6 DH21(S,P) BD SUBMISSION 11SW-B/R175-Drawing Status 製圖狀況 GS20 retevant consultants。 未經有關解問公司書而同意。不包裝製此區級內任何 次交替1954 LEGEND Do not take measurements directly from 切勿直沒從雪紙上豐度尺寸。 Check and verify all dimensions on site 符有尺寸必須在工地現場按查及審核 EXISTING FRESH WATER MAIN Read this drawing in conjunction with the specification and all other related drawings.
 此匯纸必須與根格投明實及其它有關團級一併閱讀。 IN50-2 -3 — ADH4(S/P) EXISTING STREET LIGHTING NC. 33488-A1 discrepancy found herein, 如發現內容存任何朦朧之處。應立刻通知初聲明問公元 BS2-3 BS3-2/ 11SW-B/R19 EXISTING STREET LIGHTING CABLE 11SW-B/R177 -11SW-B/R55 EXISTING HV ELECTRICITY CABLE EXISTING IN FLECTRICITY CARLE HERZOG & DEMEURON EXISTING TELECOMMUNICATION DUCT (HUTCHISON GLOBAL COMMUNICATIONS LIMITED)
EXISTING STORMWATER DRAIN EXISTING FOUL SEWER ROCCO PROPOSED FOUL SEWER Structural Engineer / RSE E & M Engineer JRP ARUP EXISTING RETAINING WALL Project ঘটি CENTRAL POLICE STATION CONSERVATION AND REVITALISATION PROJECT DH1(S,P) 11SW-B/R54 EXISTING DRILLHOLE WITH BS17-13 - 11SW-B/R178 STANDPIPE/PIEZONETER Drawing Title 劉名 BS1-1/BT1-1 MONITORING LAYOUT PLAN RS174-1/RT174-1 PROPOSED RETAINING WALL SETTLEMENT POINTS/TILTMETER PROPOSED INCLINOMETER TO BE BUILT IN BORED PILE WALL OR PIPE PILE WALL 1:300名1 K.C.Lai AL Revision博改版 00-0AP209674-G-001 M PROPOSED GROUND SETTLEMENT POINTS U∏1 ⊠ PROPOSED UTILITY MONITORING POINTS ______VM1−1 PROPOSED VIBRATION MONITORING POINTS ADH1(S/P) PROPOSED ADDITIONAL DRILLHOLE Cod Re : 00-0AP2095/4-G-001.deg

Vibration Monitoring Record (November)

| | Block 11 | | |
|-----------|----------|--------|--|
| Point | VM11-1 | VM11-2 | |
| Date | mm/s | mm/s | |
| 01-Nov-17 | 0.112 | 0.118 | |
| 02-Nov-17 | 0.105 | 0.106 | |
| 03-Nov-17 | 0.103 | 0.109 | |
| 04-Nov-17 | 0.127 | 0.104 | |
| 05-Nov-17 | Sun | day | |
| 06-Nov-17 | 0.107 | 0.109 | |
| 07-Nov-17 | 0.114 | 0.107 | |
| 08-Nov-17 | 0.110 | 0.105 | |
| 09-Nov-17 | 0.104 | 0.102 | |
| 10-Nov-17 | 0.104 | 0.105 | |
| 11-Nov-17 | 0.109 | 0.109 | |
| 12-Nov-17 | Sun | day | |
| 13-Nov-17 | 0.125 | 0.103 | |
| 14-Nov-17 | 0.110 | 0.106 | |
| 15-Nov-17 | 0.107 | 0.101 | |
| 16-Nov-17 | 0.120 | 0.121 | |
| 17-Nov-17 | 0.104 | 0.104 | |
| 18-Nov-17 | 0.107 | 0.104 | |
| 19-Nov-17 | Sun | day | |
| 20-Nov-17 | 0.105 | 0.103 | |
| 21-Nov-17 | 0.104 | 0.109 | |
| 22-Nov-17 | 0.108 | 0.103 | |
| 23-Nov-17 | 0.104 | 0.105 | |
| 24-Nov-17 | 0.107 | 0.106 | |
| 25-Nov-17 | 0.119 | 0.106 | |
| 26-Nov-17 | Sunday | | |
| 27-Nov-17 | 0.106 | 0.109 | |
| 28-Nov-17 | 0.102 | 0.102 | |
| 29-Nov-17 | 0.123 | 0.106 | |
| 30-Nov-17 | 0.116 | 0.104 | |

Vibration Monitoring Record (December)

| | Bloc | k 11 |
|-----------|----------------|---------|
| Point | VM11-1 | VM11-2 |
| Date | mm/s | mm/s |
| 01-Dec-17 | 0.112 | 0.118 |
| 02-Dec-17 | 0.105 | 0.106 |
| 03-Dec-17 | Sun | day |
| 04-Dec-17 | 0.107 | 0.101 |
| 05-Dec-17 | 0.104 | 0.123 |
| 06-Dec-17 | 0.105 | 0.112 |
| 07-Dec-17 | 0.109 | 0.108 |
| 08-Dec-17 | 0.105 | 0.106 |
| 09-Dec-17 | 0.104 | 0.109 |
| 10-Dec-17 | Sun | day |
| 11-Dec-17 | 0.109 | 0.104 |
| 12-Dec-17 | 0.104 | 0.105 |
| 13-Dec-17 | 0.107 | 0.102 |
| 14-Dec-17 | 0.115 | 0.106 |
| 15-Dec-17 | 0.103 | 0.103 |
| 16-Dec-17 | 0.110 | 0.108 |
| 17-Dec-17 | Sun | day |
| 18-Dec-17 | 0.104 | 0.102 |
| 19-Dec-17 | 0.107 | 0.106 |
| 20-Dec-17 | 0.109 | 0.102 |
| 21-Dec-17 | 0.104 | 0.105 |
| 22-Dec-17 | 0.107 | 0.106 |
| 23-Dec-17 | 0.108 | 0.105 |
| 24-Dec-17 | Sun | day |
| 25-Dec-17 | Public 1 | Holiday |
| 26-Dec-17 | Public Holiday | |
| 27-Dec-17 | 0.104 | 0.104 |
| 28-Dec-17 | 0.118 | 0.107 |
| 29-Dec-17 | 0.105 | 0.106 |
| 30-Dec-17 | 0.102 | 0.103 |
| 31-Dec-17 | Sunday | |

Vibration Monitoring Record (January)

| | Block 11 | | |
|-------------|----------|--------|--|
| Point | VM11-1 | VM11-2 | |
| Date | mm/s | mm/s | |
| 1-Jan-2018 | | | |
| 2-Jan-2018 | 0.107 | 0.108 | |
| 3-Jan-2018 | 0.114 | 0.105 | |
| 4-Jan-2018 | 0.105 | 0.104 | |
| 5-Jan-2018 | 0.102 | 0.116 | |
| 6-Jan-2018 | 0.109 | 0.104 | |
| 7-Jan-2018 | | | |
| 8-Jan-2018 | 0.105 | 0.102 | |
| 9-Jan-2018 | 0.119 | 0.105 | |
| 10-Jan-2018 | 0.107 | 0.103 | |
| 11-Jan-2018 | 0.103 | 0.110 | |
| 12-Jan-2018 | 0.116 | 0.102 | |
| 13-Jan-2018 | 0.104 | 0.107 | |
| 14-Jan-2018 | | | |
| 15-Jan-2018 | 0.106 | 0.106 | |
| 16-Jan-2018 | 0.109 | 0.103 | |
| 17-Jan-2018 | 0.106 | 0.106 | |
| 18-Jan-2018 | 0.123 | 0.102 | |
| 19-Jan-2018 | 0.105 | 0.106 | |
| 20-Jan-2018 | 0.104 | 0.103 | |
| 21-Jan-2018 | | | |
| 22-Jan-2018 | 0.112 | 0.104 | |
| 23-Jan-2018 | 0.107 | 0.107 | |
| 24-Jan-2018 | 0.104 | 0.103 | |
| 25-Jan-2018 | 0.109 | 0.108 | |
| 26-Jan-2018 | 0.102 | 0.102 | |
| 27-Jan-2018 | 0.108 | 0.102 | |
| 28-Jan-2018 | | | |
| 29-Jan-2018 | 0.102 | 0.105 | |
| 30-Jan-2018 | 0.104 | 0.103 | |
| 31-Jan-2018 | 0.109 | 0.105 | |

Annex M

Summary of Condition of Character Defining Elements, Historic Buildings and Structures

Schedule of Character Defining Elements

CENTRAL POLICE STATION, HONG KONG

SCHEDULE OF CHARACTER DEFINING ELEMENTS

This Schedule of Character Defining Elements has been prepared at the request of the Antiquities and Monuments Office (AMO) to support applications for S.6 approval under the Antiquities and Monuments Ordinance and the Environmental Impact assessment Ordinance. The levels of significance and their meanings are derived from the work of James Semple Kerr.

For each element, the level of significance is stated, together with the planned outcome and associated mitigation measure, where applicable, and the resultant impact upon the significance. Generally, only those items subject to change are noted, and the impacts should be read as negative. Where elements are deemed currently to be adverse, the impact of the changes should be read as positive.

The levels of significance and definitions as defined by Kerr are stated below. The criteria used to assess the significance of each element are, as directed by AMO: (i) the association with the operation of the Central Police Station Compound; and (ii) its architectural quality. Where these criteria conflict, the resultant assessment score is aggregated.

Each entry in the schedule is accompanied by a photograph of a sample of the item described. The location of each photograph is noted on the floor plans attached in the appendix to the schedule. Similar examples of each item can be seen by observation.

Schedule of Character Defining Elements

| | Level of significance | Meaning |
|----------|-----------------------|--|
| | Exceptional | Where an individual space or element is assessed as displaying a strong contribution to the overall significance of the place. Spaces, elements or fabric exhibit a high degree of intactness and quality, though minor alterations or degradation may be evident. |
| Positive | High | Where an individual space or element is assessed as making a substantial contribution to the overall significance of the place. Spaces, elements or fabric originally of substantial quality, yet may have undergone considerable alteration or adaption resulting in presentation which is either incomplete or ambiguous. The category also includes spaces, elements or fabric of average quality in terms of design and materials, but which exhibit a high degree of intactness. |
| | Moderate | Where an individual space or element is assessed as making a moderate contribution to the overall significance of the place. Spaces, elements or fabric originally of some intrinsic quality, and may have undergone alteration or degradation. In addition, elements of relatively new construction, where the assessment of significance is difficult, may be included. This category also includes original spaces, elements or fabric of any quality which have undergone extensive alteration or adaption. |
| | Low | Where an individual space or element is assessed as making a minor contribution to the overall significance of the place, especially when compared to other features. Spaces, elements or fabric originally of little intrinsic quality, any may have undergone alteration or degradation. This category also includes original spaces, elements or fabric of any quality which have undergone extensive alteration or adaption to the extent that only isolated remnants survive (resulting in a low degree of intactness and quality of presentation). |
| | Neutral | Where an individual space or element is assessed as having an unimportant relationship with the overall significance of the place. Spaces, elements or fabric are assessed as having little or no significance. |
| | Adverse | Where an individual space or element detracts from the appreciation of cultural significance, by adversely affecting or obscuring other significant areas, elements or items. |

Central Police Station

Schedule of Character Defining Elements

Central Police Station

| Addendum | Date |
|------------------------------|--------------|
| Item no. 10.029 edited entry | 18 June 2013 |
| Item no. 10.030 added | 18 June 2013 |

01 Police Headquarters

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|---|-----------|--------------|---|--|--------|
| 01.001 | Flat plywood ceiling lining with plain rectangular cover battens | | Adverse | Replace with T&G boarding to match existing | Not applicable | High |
| 01.002 | Plaster coving at abutments of walls and ceilings | | Low | Remove in exceptional cases eg, where adjacent new lift shaft | Cut back neatly to a square edge and ensure remaining section is secure. | Low |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|---|-----------|--------------|-------------------------------|--|--------|
| 01.003 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |
| 01.004 | Timber thresholds at external doors and internal doors between main corridor and individual rooms | | Low | Remove to enable level access | Splice extensions to door jambs, extend width of bottom rail of doors to match existing | Low |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|-----------|--------------|--|---|----------|
| 01.005 | Plaster box cornice | | Moderate | Remove in exceptional cases eg. where adjacent new lift shafts | Cut back neatly to a square edge and ensure remaining section is secure. | Moderate |
| 01.006 | Panelled doors | | Moderate | Replace where necessary to achieve fire resistance to comply with Code | Re-use where possible. Record design on survey drawings where element cannot be re- used. | Moderate |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------------------|-----------|--------------|---|---------------------------|--------|
| 01.007 | External shutters | | High | Reinstate to match existing pattern | Not applicable | High |
| 01.008 | External terraces at 1/F | | High | Overlay existing concrete paving with timber deck to provide level access | New deck to be reversible | Low |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|--|-----------|--------------|--|--|--------|
| 01.009 | Plaster ceilings on GF and LG1 | | Moderate | Install cloud ceilings to accommodate new services | Install fixed grid to minimise damage to ceiling | High |
| 01.010 | Timber door frames and architraves | | Moderate | Conceal in exceptional cases eg. where adjacent new lift shaft | Retain architrave and door frame in situ. Avoid damage to joinery. | High |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|----------------|-----------|--------------|--|---|--------|
| 01.011 | Concrete floor | | Low | Replace where new kitchens and plant rooms to be installed | Carefully remove and retain existing floorboards for re-use. Ensure controlled demolition of concrete structure and removal of debris from building to avoid damage to adjacent surfaces. Protect or carefully remove and set aside adjacent elements such as skirting boards | Low |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|-----------|--------------|--|----------------|--------|
| 01.012 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | Not applicable | High |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------|-----------|--------------|--------------------------|--|--------|
| 01.013 | Exterior decorations | | Adverse | Strip off and redecorate | Sample and analyse existing paint media; select new media to suit substrate and significance | High |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|-----------|--------------|--|---|----------|
| 01.014 | Existing door openings | | Moderate | Block opening as part of re-planning of interior | Retain existing door frame and architraves. Use framing and non-combustible sheet linings to block opening. | Moderate |
| 01.015 | Existing walls | | Moderate | Form new opening as part of re-planning of interiors | New doors and frames to be of their time to avoid confusion about provenance | Moderate |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|---|-----------|--------------|---|----------------|--------|
| 01.016 | Altered doors and windows | | Adverse | Repair or renew as necessary existing frames to match original patterns | Not applicable | High |
| 01.017 | Mezzanine floor in room 01/LG1/13 | | Adverse | Remove floor and supporting columns to re-create original double-height space | Not applicable | High |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|---|-----------|--------------|--|----------------|--------|
| 01.018 | Cast iron grilles above Service Corridor 01/LG1/35 | | High | Remove existing steel sheet covering [alterations to grilles awaiting confirmation from HdM] | | |
| 01.019 | Perforated concrete deck above lightwell | | Adverse | Remove deck and make good brickwork at abutments | Not applicable | High |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|--|-----------|--------------|--|---|----------|
| 01.020 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |
| 01.021 | Stair balustrades | | High | Balustrades to be supplemented with additional handrails and supports to mitigate non-compliance with code | New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum. | Moderate |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|----------------|-----------|--------------|--|--|--------|
| 01.022 | Main corridors | | High | Install new lighting, fire sprinklers, fire doors to comply with Fire Services Code | New fittings to be mounted in a manner that is of its time and reversible. Avoid physical intervention with existing plaster box cornices, architraves, dado rails | High |
| 01.023 | Painted signs | LOCKLEFT | High | Protect in situ | Not applicable | N/A |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|-------------|--|--------------|--|---|--------|
| 01.024 | Fixed signs | Constitution of the consti | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|---------------|-----------|--------------|--|--|--------|
| 01.025 | Pitched roofs | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material in a neutral mid-tone. | High |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|--|-----------|--------------|----------|----------------|----------|
| 01.026 | Enclosure at First Floor landing of main stair | | Adverse | Remove | Not applicable | Moderate |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|---|-----------|--------------|--|---|----------|
| 01.027 | Steel railing enclosure at FF level | | Low | Remove | Record on measured drawings and photographs | Low |
| 01.028 | Tongued and grooved flat and sloped timber boarded ceilings | | Moderate | Repair where necessary and reinstate where missing | Not applicable | Moderate |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------|-----------|--------------|---|---|----------|
| 01.029 | Modern partitions | | Adverse | Remove | Not applicable | High |
| 01.030 | Tiled dado | | High | Cut away for enlargement of existing windows to form new doorways | Cut back to joint line and adjust tiling pattern to suit new opening. New tiles to match existing sizes and colours. | Moderate |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|--|-----------|--------------|---|--|----------|
| 01.031 | Reinforced concrete canopy and sash windows | | Moderate | Remove canopy and replace sash windows with new windows to match original | Make good brickwork where canopy removed, Reinstate rendered architraves around new window to match similar window facing on West wing | Moderate |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|---|-----------|--------------|---|--|--------|
| 01.032 | Arched opening in brick wall above ceiling line | | Low | Retain insitu and use to pass through future services. Infill only where opening is within a fire compartment | Use non-combustible material to block opening. | Low |

| Element no. | Description | Photo ref | Significance | Proposal | Mitigation | Impact |
|-------------|---|-----------|--------------|--|------------|--------|
| 01.033 | Ceiling void service installation (Cast Iron Water Tank and pipework) | | Low | Remove and make good adjacent surfaces | N/A | Low |

02 Armoury

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|----------|----------------|--------|
| 02.001 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |
| 02.002 | Modern internal doors | | Adverse | Remove | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|-----------------------------------|----------------|--------|
| 02.003 | Modern partitions | | Adverse | Remove | Not applicable | High |
| 02.004 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |

Schedule of Character Defining Elements

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|--|--------|
| 02.005 | Brickwork walls enclosing rooms at GF and FF East side | | Low | Remove and reinstate verandah | Not applicable | High |
| 02.006 | Concrete floors | | Low | Selected removal to accommodate new stairs and lift shaft | Carefully form openings to ensure structural stability | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|--|---------------|--------|
| 02.007 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | No applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|---|----------------|--------|
| 02.008 | Altered doors and windows | | Adverse | Repair or renew as necessary existing frames to match original patterns | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|---------------|----------------|----------|
| 02.009 | Concrete stairs | | Adverse | Remove stairs | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------------|------------|--------------|--|---|---------|
| 02.010 | Pitched roofs | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts to reduce impact. Finish ducts in a non-reflective material that is neutral in colour and mid-tone. | High |
| 02.011 | Roof structure and tiled soffit | | High | Repair and retain. | N/A | Neutral |

03 Barracks Block

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|----------|----------------|--------|
| 03.001 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------|------------|--------------|--|---|----------|
| 3.002 | Panelled doors | | Moderate | Replace where necessary to achieve fire resistance to comply with Code | Re-use where possible. Record design on survey drawings where item cannot be re-used. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|-------------------------------------|---|--------|
| 03.003 | External shutters | | High | Reinstate to match existing pattern | Not applicable | High |
| 03.004 | Timber thresholds at external doors and internal doors between main corridor and individual rooms | | Low | Remove to enable level access | Splice extensions to door jambs, extend width of bottom rail of doors to match existing | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|--|--------|
| 03.005 | Timber spandrel panels below windows | | Low | Conceal in exceptional cases eg. where adjacent new lift shaft | Retain frame and spandrel panel where possible. Remove only where necessary in connection with replanning of interiors. Record on measured survey drawings. | Low |
| 03.006 | Timber floors | | High | Replace where new kitchens and plant rooms to be installed | Limit extent of removal as much as possible. Carefully remove and retain existing floorboards for re-use. Ensure controlled dismantling of timber structure and set aside for possible re-use. Protect or carefully remove and set aside adjacent elements such as skirting boards | Medium |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|--|---------------|--------|
| 03.007 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | No applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|--|--|--------|
| 03.008 | Exterior decorations | | Adverse | Strip off and redecorate | Sample and analyse existing paint media; select new media to suit substrate and significance | High |
| 03.009 | Block existing door openings | | Low | Block opening as part of re-planning of interior | Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|------------|--------------|--|--|--------|
| 03.010 | Form new door openings | | Low | Form new opening as part of re-planning of interiors | New doors and frames to be of their time to avoid confusion about provenance. Re-open original openings where possible. Retain original reveals and arches. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|---|----------------|--------|
| 03.011 | Altered doors and windows | | Adverse | Repair or renew as necessary existing frames to match original patterns | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|---|----------|
| 03.012 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |
| 03.013 | Stair balustrades | | High | Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code | New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------|---|--------------|--|---|--------|
| 03.014 | Painted signs | NO VISITOR WILL BE ADMITTED WITHOUT THE PERMISSION OF THE D.O. OR FORMATION COMMANDER 或官管主得未如者转探 進擅得不可許官警值當 | High | Protect in situ | Not applicable | N/A |
| 03.015 | Fixed signs | NO. 3 PLATOON R. & F CHANGING ROOM 第三隊更衣室 | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|--|----------|
| 03.016 | Pitched roofs | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone. | High |
| 03.017 | Lean-to structure adjacent North wall | | Moderate | Remove | Record on measured survey drawings. Make good walls where roof structure abuts | Moderate |

Schedule of Character Defining Elements

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|---|----------|
| 03.018 | Metal-frames windows at GF North elevation | | Adverse | Remove window frames, masonry spandrel panels below and reinstate verandah | Not applicable | High |
| 03.019 | Internal walls at Ground Floor level | | Moderate | Remove selected internal walls where strictly necessary as part of replanning of interiors | Walls of early or original date to be retained in part eg. by leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded. Record walls on measured survey dwgs. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|--|----------|
| 03.020 | Assembly rooms at centre of building (all floors) | | Moderate | Sub-divide two rooms on each floor to provide service core, comprising: lifts, toilets, plant rooms, stores | Form new sub-visions using lightweight partitions to achieve reversibility. Form straight joints at abutments with existing retained walls. Notch new partitions around existing brick corbels at high level as a reminder of current condition. | Moderate |
| 03.021 | Exposed soffits of timber floors | | Moderate | Underline existing floors to achieve specified fire resistance stated in Code | Avoid unnecessary damage to existing structure. New lining will reduce extent of intervention into existing structure. Keep level of new linings well clear of window heads. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|--|--------|
| 03.022 | Existing window frames/openings | | High | Open up selected openings to form new fire escape doors | Retain any salvageable material for possible reuse elsewhere. Retain existing window jambs intact. Cut away masonry to form door openings along same line as window jamb; do not re-bind cut brickwork. Record existing condition on measured survey drawings. | Low |
| 03.023 | Single storey outbuildings on south side | | Adverse | Demolish | Check for evidence of early route from Magistracy to Prison. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------------|------------|--------------|----------|----------------|---------|
| 03.024 | Bridge at east end | | Moderate | Retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|---|---------|
| 03.025 | Chimneypiece on Ground Floor | | Low | Repair and retain in current location | Not applicable | Neutral |
| 03.026 | Window in south wall; original dormitory space | | Moderate | Remove window and take down brickwork spandrel; subdivide space to form new fire-protected escape route. | Record existing condition on measured survey drawings. New partition wall to be reversible. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|------------------------------------|--------|
| 03.027 | Clay-tiled floor in store room adjacent stairs | | Low | Remove as part of replanning of interiors | Record on measured survey drawings | Low |

04 Dormitory Block A & B

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|-------------------------------|---|--------|
| 04.001 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |
| 04.002 | Timber thresholds at external doors and internal doors between main corridor and individual rooms | | Low | Remove to enable level access | Splice extensions to door jambs, extend width of bottom rail of doors to match existing | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|------------|--------------|--|--|----------|
| 04.003 | Plaster box cornice | | Moderate | Remove in exceptional cases where eg. where adjacent new lift shafts | Cut back neatly to a square edge and ensure remaining section is secure. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|--|---------------|--------|
| 04.004 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | No applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------|------------|--------------|--------------------------|--|--------|
| 04.005 | Exterior decorations | | Adverse | Strip off and redecorate | Sample and analyse existing paint media; select new media to suit substrate and significance | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|--|--|----------|
| 04.006 | Block existing door openings | | Moderate | Block opening as part of re-planning of interior | Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|------------|--------------|--|---|----------|
| 04.007 | Form new door openings | | Moderate | Form new opening as part of re-planning of interiors | New doors and frames to be of their time to avoid confusion about provenance | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------|------------|--------------|---|----------------|--------|
| 04.008 | Altered doors and windows | BLOCK B | Adverse | Repair or renew as necessary existing frames to match original patterns | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|----------------|--------|
| 04.009 | Window frames in arcades of North and East elevations | | Adverse | Remove window frames and make good masonry reveals and reinstate verandah | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|-----------------------------------|----------------|--------|
| 04.010 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------|------------|--------------|---|---|----------|
| 04.011 | Stair balustrades | | High | Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code | New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------------------|------------|--------------|---------------------------------|--|----------|
| 04.012 | Stair from First to Second Floor | | High | Replace stair to improve safety | New stair to be built of steel to comply with Code and to distinguish it as being "of its time". | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------------|--|--------------|--|---|--------|
| 04.013 | External verandahs | The state of the s | High | Install new lighting, fire sprinklers, fire doors to comply with Fire Services Code, extract ducting to external walls | New fittings to be mounted in a manner that is of its time and reversible. Avoid physical intervention with existing plaster box cornices in rooms, architraves, dado rails. Position outlet grilles in extneral walls on centreline of arcade arches and above structural arch | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------|------------|--------------|--|---|--------|
| 04.014 | Painted signs | BLOCK A | High | Protect in situ | Not applicable | N/A |
| 04.015 | Fixed signs | | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------|------------|--------------|--|--|--------|
| 04.016 | Pitched roofs | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour. | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|-------------------------------|----------------|--------|
| 04.017 | Toilets at ends of verandahs | | Adverse | Remove and make good finishes | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------------|------------|--------------|---------------------------------------|---|----------|
| 04.018 | Partitions at GF Dormitory A | | High | Remove to make way for Interpretation | Prepare measured drawings and photographs before removal. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------------|------------|--------------|---|----------------|--------|
| 04.019 | Switchgear in old porch 04/G/13 | | Adverse | Open up porch, remove electrical switchgear and make good | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|----------------|--------|
| 04.020 | Flat plywood ceiling lining with plain rectangular cover battens | | Adverse | Replace with T&G boarding to match existing | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|---|----------|
| 04.021 | Steps up to doorway on FF verandah | EXIT | Moderate | Remove steps and doorway to form new fore escape route | Record steps and doorway on measured drawings | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|--|--------|
| 04.022 | Timber boarded floors with moulded skirtings | | High | Retain all boarded floors and skirtings | Reinstate floor boards and skirtings after fire proofing works | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------|------------|--------------|---|--|--------|
| 04.023 | Cantilever balconies | | High | Retain and repair as necessary. Reinstate balcony on west elevation. | Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--------------------------------|----------------|---------|
| 04.024 | Clay tile floor | | Low | Retain and repair as necessary | Not applicable | Neutral |
| 04.025 | Matched- boarded ceiling with perforated border | | Moderate | Repair and retain insitu | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--------------|------------|--------------|--------------------------|----------------|---------|
| 04.026 | Ceiling rose | | Low | Repair and retain insitu | Not applicable | Neutral |

06 Dormitory C

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|--|--------|
| 06.001 | Granite thresholds at external doors | | Low | Retain; install timber deck flush with level of step where necessary | Avoid alteration to step. | Low |
| 06.002 | Pitched roof | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone. | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------|------------|--------------|--|--|----------|
| 06.003 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | Not applicable | High |
| 06.004 | Exterior decorations | | Adverse | Strip off and redecorate | Sample and analyse existing paint media; select new media to suit substrate and significance | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|----------|---|-------------------|
| 06.005 | Altered doors and windows | | Adverse | Adverse | Repair or renew as necessary existing frames to match original patterns | Not applicable |
| 06.006 | External airconditioning units and other external services | | Adverse | Adverse | Remove and make good brickwork | Not applicable |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------|--|--------------|--|---|--------|
| 06.007 | Painted signs | PECKC. | High | Protect in situ | Not applicable | N/A |
| 06.008 | Fixed signs | 衛生署 DEPARTMENT OF HEALTH 中央警署診療所 POLICE MEDICAL POST CENTRAL POLICE STATIN | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------|------------|--------------|---------------------------------|--|--------|
| 06.009 | Cantilever balconies | | High | Retain and repair as necessary. | Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective. | Low |
| 06.010 | Iron balustrades | | High | Retain and repair as necessary. | Avoid highly visible intervention to enhance structural integrity and/or compliance with building codes. Restrict access if necessary to achieve this objective. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|---|----------|
| 06.011 | Perforated margin at perimeter of ceiling | EXIT ED | Low | Repair and retain. | Where fire-proofing of floor is required, use a product that can be installed within the floor void, leaving the ceiling lining intact. | Low |
| 06.012 | Block existing door openings | EXIT | Moderate | Block opening as part of re-planning of interior | Retain existing door frame and architraves. Use framing and non-combustible sheet linings to block opening. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|------------|--------------|---|---|----------|
| 06.013 | Form new door openings | | Moderate | Form new opening as part of re-planning of interiors | New doors and frames to be of their time to avoid confusion about provenance | Moderate |
| 06.014 | Stair balustrades | | High | Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code | New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------|------------|--------------|---|--|----------|
| 06.015 | Timber floors | | High | Retain all boarded floors and skirtings | Reinstate floor boards and skirtings after fire proofing works | Low |
| 06.016 | Vinyl tile floor | | Adverse | Remove tiles; renew boarded floor boards if necessary | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------------|------------|--------------|---------------------------------------|---|--------|
| 06.017 | Batten and panel ceiling lining | | Low | Replace with lath and plaster ceiling | Not applicable | Low |
| 06.018 | Exposed roof covering | | Moderate | Retain as existing | Consider insulating between upper and lower layers of roof tiles to provide thermal insulation and vapour barrier | Low |

07 Dormitory D

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|--|---|--------|
| 07.001 | Pitched roofs | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone. | High |
| 07.002 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | No applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|---|--|--------|
| 07.003 | Exterior decorations | | Adverse | Strip off and redecorate | Sample and analyse existing paint media; select new media to suit substrate and significance | High |
| 07.004 | Altered doors and windows | | Adverse | Repair or renew as necessary existing frames to match original patterns | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|-----------------------------------|----------------|--------|
| 07.005 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |
| 07.006 | Clothes drying racks | | Adverse | Remove | Not applicable | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|--|--------|
| 07.008 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |
| 07.009 | Corbelled brickwork at perimeter of room | | Low | Remove in exceptional cases where eg. where adjacent new lift shafts | Cut back neatly to a square edge and ensure remaining section is secure. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|------------------------------------|---|--------|
| 07.010 | Plywood floor | | Adverse | Replace with hardwood floor boards | Not applicable | High |
| 07.011 | Timber thresholds at external doors and internal doors between main corridor and individual rooms | | Low | Remove to enable level access | Splice extensions to door jambs, extend width of bottom rail of doors to match existing | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|------------|--------------|---|---|----------|
| 07.012 | Form new door openings | | Moderate | Form new opening as part of re-planning of interiors | New doors and frames to be of their time to avoid confusion about provenance | Moderate |
| 07.013 | Stair balustrades | | High | Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code | New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------|---|--------------|--|---|--------|
| 07.014 | Fixed signs | P 学 子 分 体 所 Control Price Station Redicts But | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------|------------|--------------|------------------------------------|---|----------|
| 07.015 | Exposed roof tiling | | Moderate | Retain as existing | Consider insulating between upper and lower layers of roof tiles to provide thermal insulation and vapour barrier | Low |
| 07.016 | Concrete floor | | Adverse | Overlay with hardwood floor boards | Not applicable | Moderate |

08 Ablutions Block

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|--|--|----------|
| 08.001 | Panelled doors | | Low | Replace where necessary to achieve compliance with Building Code | Re-use where possible. Record design on survey drawings where element cannot be re-used. | Moderate |
| 08.002 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | No applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|--|--|----------|
| 08.003 | Exterior decorations | | Adverse | Strip off and redecorate | Sample and analyse existing paint media; select new media to suit substrate and significance | High |
| 08.004 | Block existing door openings | | Moderate | Block opening as part of re-planning of interior | Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------|------------|--------------|----------|--|---------|
| 08.005 | Timber roof structure | | High | Retain | Not applicable | Neutral |
| 08.006 | External stair at west end | | Moderate | Retain | Repair as necessary. Alter balustrade to achieve reasonable level of operational safety. Restrict access to repairs and maintenance and means of escape. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|--|--------------|-----------------------------------|----------------|--------|
| 08.007 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |
| 08.008 | Painted signs | NO VISITOR WILL BE ADMITTED WITHOUT THE PERMISSION OF THE D. D. OR FORMANION COMMANDER 支管主導体和者珍様 連接将不可計官擊血當 | High | Protect in situ | Not applicable | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------------|------------|--------------|---|---|--------|
| 08.009 | Wire mesh screens | | Adverse | Remove | Not applicable | Low |
| 08.010 | Internal walls and concrete floors | | Low | Remove and rebuild in new configuration to suit new use | Ensure retained facades are fully supported during construction operations. Protect retained walls against damage during demolition works. Install new walls and floors to respect fenestration; avoid | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--------------------------|----------------|--------|
| | | | | | clashes. | |
| 08.011 | Cantilever balconies on north side | | Moderate | Repair and retain insitu | Not applicable | |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------------------------|------------|--------------|--|--|--------|
| 08.012 | Bridge access to Barrack Block | | Moderate | Retain | Repair as necessary. Alter balustrade to achieve reasonable level of operational safety. Restrict access to repairs and maintenance and means of escape. | Low |
| 08.013 | Balcony balustrades | | Low | Repair as necessary and retain. Remove selected sections to enable installation of new bridge connections to Barrack Block. | Avoid removal of associated iron columns. Form interventions at selected positions so as to maintain the rhythm of the balustrades and ensure proper support at ends. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|---|--------|
| 08.014 | Single-storey outbuilding with pitched roof over | | Low | Demolish to make way for new loading bay. | Record on measured survey drawings. Infill existing internal opening leaving reveals exposed. Tooth-in new brickwork at abutments after existing walls removed. Salvage cast iron columns for possible re-use. | Low |
| 08.015 | Corrugated steel sheet on balcony balustrades | | Adverse | Remove | Not applicable | Low |

Schedule of Character Defining Elements

Central Police Station

09 Magistracy

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|----------|----------------|--------|
| 09.001 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |
| 09.002 | Modern partitions | | Adverse | Remove | Not applicable | N/A |

Schedule of Character Defining Elements

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|------------|--------------|--|---|----------|
| 09.003 | Internal walls | | Moderate | Remove selected internal walls where strictly necessary as part of replanning of interiors | Walls or early or original date to be retained in part eg. By leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded, as evidence of the current condition. | Moderate |
| 09.004 | Plaster box cornice | | Moderate | Remove in exceptional cases eg. Where adjacent new lift shafts | Cut back neatly to a square edge and ensure remaining section is secure. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------|------------|--------------|--|--|----------|
| 09.005 | Panelled doors | | Moderate | Replace where necessary to achieve fire resistance to comply with Code | Re-use where possible. Record design on survey drawings where element cannot be re-used. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|--|--|----------|
| 09.006 | Block existing door openings | | Moderate | Block opening as part of re-planning of interior | Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening. | Moderate |
| 09.007 | Form new door openings | | Moderate | Form new opening as part of re-planning of interiors | New doors and frames to be of their time to avoid confusion about provenance | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------|--|--------------|---|---|----------|
| 09.008 | Stair balustrades | | High | Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code | New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum. | Moderate |
| 09.009 | Fixed signs | WINDOWS DEPARTMENT RESOLUTION DEPARTMENT RE | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|--|--------|
| 09.010 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |
| 09.011 | Pitched roofs | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone. | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------------|------------|--------------|---|---|--------|
| 09.012 | Rainwater goods | | Moderate | Replace with larger sizes/closer spacing to improve performance | Use cast iron to match original pattern Make good all redundant fixing holes | High |
| 09.013 | Metal walkways across lightwell | | Adverse | Remove walkways and make good brickwork at abutments | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|----------------|----------|
| 09.014 | Altered doors and windows | | Adverse | Repair or renew as necessary existing frames to match original patterns | Not applicable | High |
| 09.015 | Sloping canopy over external stair on west side | | Adverse | Remove canopy and supporting structure | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|-----------------------------------|---------|
| 09.016 | Single storey secure shelter at North West corner | | Low | Demolish | Make good brickwork at abutments. | Low |
| 09.017 | Iron railing adjacent south side of item 09.016 above | | Moderate | Retain; including remains of bars (now removed) between existing railings and east side of Barracks Block. | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------------|------------|--------------|---|--|--------|
| 09.018 | Public toilets in 09/LG1/17, 24 | | Adverse | Strip out sanitaryware, and fit-out for pottery display/service access. Form new door openings in east walls. | Retain existing door openings and metal- barred gates. Retain external granite steps and existing ground level. | Low |
| 09.019 | Cell doors | | High | Re-open to provide access to Retail space | Retain existing iron gate | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------------------------|------------|--------------|---|---|----------|
| 09.020 | Meeting room at G/02-05 | | Moderate | Remove timber panelling from walls and sub divide to form new toilets and lift shaft | Record existing wall linings, and any earlier lining behind, on measured survey drawings. | Moderate |
| 09.021 | Lobbies within entrance hall G/12 | | Adverse | Remove | Not applicable | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------|------------|--------------|---|----------------|---------|
| 09.022 | Public galleries on FF | | Adverse | Strip out plant, remove partition walls and restore galleries | Not applicable | High |
| 09.023 | Chimney piece | | Moderate | Retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------------------|------------|--------------|---|---|----------|
| 09.024 | Lanterns above entrance hall | | Adverse | Remove existing lanterns and install single lantern | Not applicable | Moderate |
| 09.025 | Boarded ceilings on Second Floor | | High | Repair and retain where possible | Limit extent of penetrations as far as practicable. Record on measured survey drawings where ceilings have exceptionally to be removed. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|--|---------|
| 09.026 | Iron gates at top of external stair | | Moderate | Retain | No applicable | Neutral |
| 09.027 | Iron balustrade adjacent terrace at First Floor east side | | High | Retain; install structural glass balustrade inboard of ironwork to provide compliance with Building Codes | Avoid penetration of existing tiled pavement when fixing glass balustrade. | Low |

10 Assistant Superintendent's Office

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|--|--|----------|
| 10.001 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |
| 10.002 | Plaster box cornice | | Moderate | Remove in exceptional cases eg. Where adjacent new lift shafts | Cut back neatly to a square edge and ensure remaining section is secure. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------------|------------|--------------|--|--|----------|
| 10.003 | Panelled doors and linings | No. 1272. | Moderate | Replace where necessary to achieve fire resistance to comply with Code | Re-use where possible. Record design on survey drawings where element cannot be re-used. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--------------------------------|---|--------|
| 10.004 | Timber boarded floor with moulded skirtings | | High | Repair as necessary and retain | Lift carefully and refix upon completion of fire- proofing and services installation | Low |
| 10.005 | Exterior decorations | | Adverse | Strip off and redecorate | Sample and analyse existing paint media; select new media to suit substrate and significance | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|--|--|----------|
| 10.006 | Block existing door openings | | Moderate | Block opening as part of re-planning of interior | Retain existing door frame and architraves. Use framing and noncombustible sheet linings to block opening. | Moderate |
| 10.007 | Form new door openings | | Moderate | Form new opening as part of re-planning of interiors | New doors and frames to be of their time to avoid confusion about provenance | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|----------------|--------|
| 10.008 | Altered doors and windows | | Adverse | Repair or renew as necessary existing frames to match original patterns | Not applicable | High |
| 10.009 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------|------------|--------------|---|---|----------|
| 10.010 | Stair balustrades | | High | Balustrades to be supplemented with additional handrails and supports to mitigate noncompliance with code | New fittings to be of their time and made reversible. Physical intervention to existing stairs and balustrades to be kept to the minimum. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------|---|--------------|--|--|--------|
| 10.011 | Fixed signs | は、大きない。 は、たるない。 は、なない。 は、なない。 は、なななななななななななななななななななななななななななななななななななな | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |
| 10.012 | Pitched roofs | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone. | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------|------------|--------------|--|---|----------|
| 10.013 | Internal walls | | Moderate | Remove selected internal walls where strictly necessary as part of replanning of interiors | Walls or early or original date to be retained in part eg. By leaving a "nib" where the wall is bonded to another wall. At the point where the wall is cut away, form the cut-line on the line of a vertical joint in alternate courses. Bricks in the remaining courses to be left "as cut", and not rebonded, as evidence of the current condition. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|--|----------|
| 10.014 | Partitions on SF | | Moderate | Remove partitions | Record partitions on measured drawings | Moderate |
| 10.015 | Blocked windows on south elevation of south-east wing | | Adverse | Re-open window openings and reinstate window frames and glazing | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|--|---------|
| 10.016 | Open-joisted ceiling on Ground Floor of south- east wing | | Moderate | Underline floor to provide fire protection. | Avoid intrusive alteration. Use fire-proofing products and methods that enable existing structure and boarding to be retained. | Low |
| 10.017 | Moulded timber picture rail | | Low | Repair and retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|---|--------|
| 10.018 | Timber roof structure above south-east wing | | Moderate | Repair as necessary and retain | Avoid intrusive alteration. Retain open appearance/ | Low |
| 10.019 | Timber stair | | Moderate | Underline with fire- resisting lining | Repair as necessary and retain. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|---|--------|
| 10.020 | Clay/terrazzo tile floor on Ground Floor and steps | | Adverse | Adjust levels to enable level access and replace floor finish | Not applicable | Low |
| 10.024 | Granite wall on North elevation | | High | Construct new external steps adjacent wall | Keep new stair clear of wall; avoid any physical connection between steps and wall. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|--|----------|
| 10.025 | Single storey outbuilding at South East corner | | Moderate | Demolish outbuilding and make good at abutments | Record outbuilding on measured drawings | Low |
| 10.026 | Blocked archway on East elevation | | Adverse | Demolish infilling and reopen archway | Protect original arch and jambs against damage during demolition | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------|------------|--------------|--------------------------------|--|---------|
| 10.027 | Chimney on east elevation | | Low | Retain | Not applicable | Neutral |
| 10.028 | Cantilever balconies | | High | Repair as necessary and retain | Avoid intrusive interventions. Restrict access if necessary to retain existing appearance. | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--------------------------------|----------------|----------|
| 10.029 | Steps on east elevation | | Moderate | Repair as necessary and retain | Not applicable | Neutral |
| 10.030 | Decorative metal screen (See also item 10.026) | | Low | Repair and retain | Not applicable | Positive |

11 A Hall

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------|------------|--------------|--|---|--------|
| 11.001 | Form new door openings | | Low | Form new opening as part of re-planning of interiors | New doors and frames to be of their time to avoid confusion about provenance | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|-----------------------------------|----------------|--------|
| 11.002 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |
| 11.003 | Painted signs | AHALL | High | Protect in situ | Not applicable | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|---|--------------|--|---|--------|
| 11.004 | Fixed signs | 多生 小心地滑 CAUTION SLIPPERY FLOOR | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |
| 11.005 | Concrete stairs | | Low | Remove and rebuild as part of re-planning of interiors | None | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------------|------------|--------------|--|--|--------|
| 11.006 | Flat roof | | Low | Form new rooftop extension at West end to accommodate fire escape stair | Form straight joint at abutment with building 08 Ablutions Block | Low |
| 11.007 | Security screen at roof level | | Low | Remove | Record on measured survey drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|--|----------------|--------|
| 11.008 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|---|---|--------|
| 11.009 | Rainwater goods | | Low | Remove embedded cast iron pipework set into wall to reduce long term maintenance burden | Record on measured survey drawings. Make good cavity. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--------------|------------|--------------|-------------------|----------------|---------|
| 11.010 | Timber doors | | Low | Repair and retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|------------------------------------|---------|
| 11.011 | Security screen and door at First Floor | EXITHO | Low | Remove | Record on measured survey drawings | Low |
| 11.012 | Door thresholds and plinth | | Low | Retain; remove paint media from plinth and brickwork | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|----------|----------------|--------|
| 11.013 | Metal louvres on window openings | | Adverse | Remove | Not applicable | Low |

12 B Hall

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------|------------|--------------|---|---|----------|
| 12.001 | Flat roof | | Moderate | Repair and retain | Avoid roof penetrations as far as possible | Low |
| 12.002 | Cells at GF level | | High | Remove cells in selected locations to accommodate new North-South route across site | Record existing layout on measured survey drawings. Limit number of cells affected to the minimum necessary. Retain floor structure above. Retain remainder of cells at this level for interpretation | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|-----------------------------------|----------------|--------|
| 12.003 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |
| 12.004 | Painted signs | | High | Protect in situ | Not applicable | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|--|--------------|--|---|--------|
| 12.005 | Fixed signs | The state of the s | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |
| 12.006 | Rainwater goods | | Adverse | Replace with cast iron in pattern to match original and in correct locations | Not applicable | High |

Schedule of Character Defining Elements

Central Police Station

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|----------|----------------------------------|---------|
| 12.007 | Corbelled brickwork at high level in cells | | Low | Retain | Not applicable | Neutral |
| 12.008 | Barbed wire | | Moderate | Remove | Record wire on measured drawings | Low |

Schedule of Character Defining Elements

Central Police Station

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------|------------|--------------|---|--|----------|
| 12.009 | External walls | | Moderate | Form openings in North and South walls in conjunction with new North-South route across site | Cut brickwork to form openings in North and South walls; do not re-bond brickwork. | Moderate |

13 C Hall

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|----------|----------------|----------|
| 13.001 | External airconditioning units and other external services | | Adverse | Remove | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|----------|----------------|---------|
| 13.002 | Door to Ladder Store | | Low | Retain | Not applicable | Neutral |
| 13.003 | Security bars at window openings | | Low | Retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--------------|------------|--------------|----------|---|---------|
| 13.004 | Flat roof | | Low | Retain | Avoid roof penetrations as far as possible. | Low |
| 13.005 | Eaves detail | | Low | Retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------------------|------------|--------------|----------|----------------|---------|
| 13.006 | Cantilever reinforced concrete canopy | | Low | Retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--------------------------|--|--------------|--|---|--------|
| 13.007 | Internal partition walls | | Low | Remove as part of replanning of interiors | Record on measured survey drawings | Low |
| 13.008 | Fixed signs | Note that the second of the se | Low-High | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | N/A |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------|------------|--------------|-----------------------|---|---------|
| 13.009 | Metal window frames | | Moderate | Repair and retain | Not applicable | Neutral |
| 13.010 | Internal security screens | | Moderate | Retain where possible | Where necessary record on measured survey drawings prior to removal | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|---|--------|
| 13.011 | Coving at abutments between RC beams and walls | | Low | Avoid penetrations for services installations as far as possible. | Cut away neatly for services penetrations and make good at abutments. | Low |
| 13.012 | Communal cells at Ground Floor | | Moderate | Remove as part of re- planning of interiors | Record on measured survey drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|------------------------------------|---------|
| 13.013 | Rooflight and security bars over communal cells | | Moderate | Remove as part of replanning of interiors | Record on measured survey drawings | Low |
| 13.014 | Granite threshold at external door openings | | Low | Retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--------------------------------|----------------|---------|
| 13.015 | Timber boarded doors with fanlight over | | Low | Repair as necessary and retain | Not applicable | Neutral |
| 13.015 | Vinyl tile floor | | Adverse | Replace | Not applicable | Low |

Schedule of Character Defining Elements

Central Police Station

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------|------------|--------------|----------|------------|--------|
| | | | | | | |

14 D Hall East Wing

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|--|--------|
| 14.001 | West entrance at Lower Ground Floor | | Moderate | Retain as public entrance at this level. | Retain security gate and granite threshold. Adjust adjacent ground level as necessary to achieve barrier-free access. Pin gate back against adjacent wall in the open position if necessary. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|----------|---|--------|
| 14.002 | Half-round headed doorway and side lights | | Moderate | Retain | Remove air duct and make good masonry above arch. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|---|--------|
| 14.003 | Granite surround to cells (generally north side, alternating with brick surrounds – see next item) | 3 | Moderate | Retain door surround and gate wherever possible. | Pin back gate against wall. Remove paint media to expose granite material. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|----------------------------|--------|
| 14.004 | Brick reveals with bull-nosed arrisses and segmental arch over (generally north side, alternating with granite surrounds – see previous item) | | High | Retain door surround and gate wherever possible | Pin back gate against wall | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|--|--------|
| 14.005 | Arched opening at East end First Floor | | Low | Retain as existing | Not applicable | Low |
| 14.006 | Concrete floor generally at Lower Ground Floor | | Low | Excavate entire floor to install piled underpinning | Record levels on measured survey drawings. Install new floor at the same level. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--|--|--------|
| 14.007 | Part-blocked windows at Lower Ground Floor - extent of blocking varies. | | Moderate | Open up window opening to full extent. | Record existing condition on measured survey drawings. Add further detail during demolition works. | Low |
| 14.008 | External granite stair from Lower Ground to Ground Floor level | | Moderate | Remove stair to make way for new stair in similar position | Review design proposals to see whether existing stair can be retained. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|---|---|--------|
| 14.009 | Ashlar pattern on external walls | | Moderate | Form new openings for entrance/exit to building | Set out new openings to cause minimum disruption to ashlar pattern. Record existing pattern on measured survey drawings. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|----------------------------------|----------------|---------|
| 14.010 | Blocked doorway at south-east corner | | Low | Preserve blocked opening intact. | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--------------------------------|------------|--------------|---------------|--|---------|
| 14.011 | Metal security gate and screen | | Low | Retain insitu | Pin gate in open position if necessary | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--|----------------|----------|
| 14.012 | Half-round headed doorway and side lights at Ground Floor west end | | Moderate | Retain insitu | Not applicable | Neutral |
| 14.013 | Structural steelwork bracing and temporary access stair | | Adverse | Remove upon completion of underpinning | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|-----------------------------|--------|
| 14.014 | RC staircase at north-east corner | | Low | Remove | Record on measured drawings | Low |
| 14.015 | Vinyl tile floor on suspended timber floor | | Adverse | Remove vinyl tiles and restore boards if possible; alternatively, replace boards with new timber to match other boarded floors elsewhere on the site. | Not applicable | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------------|------------|--------------|---------------|--|--------|
| 14.016 | Cell walls at Ground Floor | | Moderate | Retain insitu | Use existing door openings wherever possible. Avoid further alteration to existing altered openings where feasible. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|--|---------|
| 14.017 | Mortuary | | High | Preserve insitu | Avoid any service penetrations from adjacent spaces | Neutral |
| 14.018 | Brickwork surrounds to doorways with segmental arches over | | Moderate | Increase width in selected locations to allow wheelchairs to pass | Record on measured survey drawings. Limit interventions as far as possible. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|--|--------|
| 14.019 | Granite surrounds to doorways with lintels over | | Moderate | Increase width in selected locations to allow wheelchairs to pass | Record on measured survey drawings. Limit interventions as far as possible. | Low |
| 14.020 | Flat ceilings at Ground Floor | A | Low | Form penetrations for services installations where necessary | Avoid disruption of beams. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------|------------|--------------|---------------|----------------|---------|
| 14.021 | Arched opening at east end | | Low | Retain insitu | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------|------------|--------------|---------------|----------------|---------|
| 14.022 | Top-lit central hall | | High | Retain insitu | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---------------|----------------|---------|
| 14.023 | Arches across central hall at First Floor | | Moderate | Retain insitu | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|------------------------|---|--------|
| 14.024 | Inset security gate and screen in First Floor cells | | Low | Remove to suit new use | Remove where necessary. Record on measured drawings. | Low |

14 D Hall West Wing

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------|------------|--------------|------------------------------|-----------------------------|--------|
| 14.030 | Main stair | | High | Remove wire mesh and framing | Record on measured drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|-------------------------------------|------------------------------------|----------|
| 14.031 | Brick vault over central hall at Ground Floor | | High | Retain insitu | Not applicable | Neutral |
| 14.032 | Terrazzo floor in central hall at Ground floor | | Moderate | Remove to enable piled underpinning | Record on measured survey drawings | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|--|---------------------------------|---------|
| 14.033 | Brick vaults above cells | | High | Retain insitu | Avoid penetrations for services | Neutral |
| 14.034 | Cell walls (later additions) | | Moderate | Remove where necessary to accommodate new cafe | Record on measured drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|--------------------------------|------------------------------------|--------|
| 14.035 | Brickwork spandrels below cell windows on south side at Ground Floor | | Moderate | Remove to accommodate new cafe | Record on measured survey drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|--------------------------------|---|----------|
| 14.036 | Cell walls flanking central hall | | High | Remove to accommodate new cafe | Record on measured survey drawings. Retain selected cells for interpretation purposes. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------|------------|--------------|-------------------------------------|------------------------------------|--------|
| 14.037 | Cell floors | | Low | Remove to enable piled underpinning | Record on measured survey drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--------------------------------|------------------------------------|--------|
| 14.038 | Partition wall across central hall at Ground Floor | | Low | Remove to accommodate new cafe | Record on measured survey drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---------------------------------------|----------------|---------|
| 14.039 | Granite pavement in cross-passage between East and West Wings | | Moderate | Repair as necessary and retain insitu | Not applicable | Neutral |
| 14.040 | Granite threshold at doorway between cross- passage and East Wing | | Moderate | Retain insitu | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---------------|---------------------------------|---------|
| 14.041 | Brick vault over cross-passage | | High | Retain insitu | Avoid any services penetrations | Neutral |
| 14.042 | Granite floor in central hall at First Floor | | Moderate | Retain insitu | Repair where necessary | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|--------------------------|---|---------|
| 14.043 | Cell walls flanking central hall at First Floor | | High | Retain insitu | Not applicable | Neutral |
| 14.044 | Brickwork spandrels below cell windows at Second Floor | | Moderate | Remove to enable new use | Record on measured drawings. Confine changes to one elevation, north or south. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---------------|----------------|---------|
| 14.045 | Metal security screen adjacent main stair | | Moderate | Retain insitu | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---------------|----------------|---------|
| 14.046 | Double-height central hall at Second Floor | | High | Retain insitu | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---------------|----------------|----------|
| 14.047 | View ports adjacent entrance doors | | Moderate | Retain insitu | Not applicable | Neutral |
| 14.048 | Services installations | | Adverse | Remove | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|---|--------|
| 14.049 | Metalwork and structural steel framing on exterior (typical) | | Adverse | Remove | Not applicable | High |
| 14.050 | Blind arcade, south elevation | | Low | Remove infill brickwork within arched openings at ground level to enable new cafe | Record on measured survey drawings. Observe and record any evidence that brickwork infills were built at the same time as the arched openings or added later | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|---|-----------------------------|---------|
| 14.051 | Blind arcade, north elevation | | Low | Retain insitu | Not applicable | Neutral |
| 14.052 | Fence wall, east end of D Hall Yard | | Low | Remove to reinstate access to granite stair to Lower Ground Floor level | Record on measured drawings | Low |

15 E Hall

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|--|--------------|--|------------------------------------|--------|
| 15.001 | Dividing walls at Lower Ground Floor | HAIR AND THE PARTY OF THE PARTY | Moderate | Remove to enable multi- purpose use | Record on measured survey drawings | Low |
| 15.002 | Dividing walls at Lower Ground Floor | | Moderate | Remove to enable multi- purpose use | Record on measured survey drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|---|------------------------------------|--------|
| 15.003 | Staircase within Laundry Yard | | Moderate | Remove to enable construction of Arbuthnot Wing | Record on measured survey drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|----------|------------------------------------|----------|
| 15.004 | Services installations | Tart | Adverse | Remove | Not applicable | Moderate |
| 15.005 | Metal louvres over cell window openings | | Low | Remove | Record on measured survey drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|------------|--------------|-------------------------------|---|--------|
| 15.006 | Raised ground level adjacent entrance | | Low | Remove to enable level access | Record on measured survey drawings | Low |
| 15.007 | Access balconies and apertures | | Moderate | Retain apertures | Provide temporary closure as required for operational reasons | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------|------------|--------------|----------|--|--------|
| 15.008 | Central staircase | | High | Retain | Provide secondary staircase within cell blocks to achieve code compliance | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|----------|------------------------------------|---------|
| 15.009 | Cell walls flanking central hall | | High | Retain | Pin back cell doors against walls. | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---------------------------|------------|--------------|----------|---|----------|
| 15.010 | Services installations | Add BODDO | Adverse | Remove | Not applicable | Moderate |
| 15.011 | Balcony balustrades | | Moderate | Retain | Install wire net across aperture to avoid need to upgrade balustrade to meet Building Code requirements | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------------------|------------|--------------|----------|----------------|---------|
| 15.012 | Second Floor central hall | | High | Retain | Not applicable | Neutral |

17 F Hall

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------------------------|------------|--------------|----------|----------------|--------|
| 17.001 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------|------------|--------------|---|--|--------|
| 17.002 | Rainwater goods | | Low | Remove existing RWPs and install new RWPs externally on North and South Elevations | Improve roof drainage to avoid ponding | Low |
| 17.003 | Exterior decorations | | Adverse | Strip off and redecorate | Sample and analyse existing paint media; select new media to suit substrate and significance | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|---|--------------|--|---|----------|
| 17.004 | External airconditioning units and other external services | | Adverse | Remove and make good brickwork | Not applicable | High |
| 17.005 | Fixed signs | PRISONERS' PRIVATE CLOTHING STORE 犯人私家衣服儲藏室 | Moderate | Remove and refix/display in visitors' centre/discard | Record each sign and assess significance individually and treat accordingly | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|------------------------------|----------|
| 17.006 | Security screen at First Floor entrance | | Low | Remove | Record on measured drawings | Low |
| 17.007 | Metal windows | | Moderate | Remove at First Floor to accommodate gallery space and block structural openings with blockwork | Record on measured drawings. | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|------------------|------------|--------------|-------------------------------------|-----------------------------|----------|
| 17.008 | Fixed furniture | | Moderate | Remove to accommodate gallery space | None | Low |
| 17.009 | Security screens | | Moderate | Remove to accommodate gallery space | Record on measured drawings | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|-----------------------------|----------|
| 17.010 | Timber windows | | Moderate | Remove at First Floor to accommodate gallery space and block structural openings with blockwork | Record on measured drawings | Moderate |
| 17.011 | Communal washing/lavatory facilities | | Moderate | Remove to accommodate gallery space | Record on measured drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------------------------|------------|--------------|---|-----------------------------|--------|
| 17.012 | Blocked up lantern light | | Low | Unblock lantern and fit glazing | Record on measured drawings | Low |
| 17.013 | Security gates at Ground openings | | Moderate | Remove to enable access to Ground Floor gallery space | Record on measured drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------------|------------|--------------|---|--|----------|
| 17.014 | Interview booths | | High | Remove to accommodate new gallery | Rebuild in new location | Moderate |
| 17.015 | External stair to First Floor | | Moderate | Upgrade balustrade to comply with Building Code | Record on measured drawings. Supplement existing balustrade elements with minimal elements if necessary. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|----------------------------|------------|--------------|---------------------|--|--------|
| 17.016 | Ground Floor main entrance | | Low | Retain as existing. | Keep fixed shut if not required for operational use. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|---|--|--------------|-------------------------------------|-----------------------------|--------|
| 17.017 | Security screen at Ground Floor main entrance | STATE AND TO STATE OF | Low | Remove to accommodate gallery space | Record on measured drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|---|---------|
| 17.018 | Blue Entrance Gate (facing Old Bailey Street) | | High | Retain in situ | Maintain in working order | Neutral |
| 17.019 | Blue Entrance Gate (inner) and enclosed yard | | Moderate | Retain gate and enclosing walls and roof in situ; remove cupboards. | Repair and maintain gate in working order | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---------------------------------|---|--------|
| 17.020 | Blue Entrance Gate (inner) facing Prison Yard | | Moderate | Retain gate and enclosing frame | Repair and maintain in working order | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-------------|------------|--------------|----------|--|--------|
| 17.021 | Barbed wire | | Moderate | Remove | Record on measured drawings. Make good fixing points where attached to brickwork. | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|--|------------|--------------|---|-----------------------------|--------|
| 17.022 | Metal security bars at windows | | Moderate | Remove as part of blocking up window openings to accommodate gallery space at First Floor | Record on measured drawings | Low |
| 17.023 | External toilets at Ground Floor adjacent East elevation | | Low | Remove | Record on measured drawings | Low |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|-------------|-----------------|------------|--------------|---------------------------------|--|--------|
| 17.024 | Open Visit Room | | Low | Space reallocated to other uses | Record on measured drawings. Salvage entrance sign and re-use in new layout of interview booths. | Low |

19 Bauhinia House

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|---------------|------------|--------------|--|---|---------|
| 19.001 | Pitched roofs | | High | New penetrations through roofs for ventilation ducts and other services | Arrange new penetrations so that they conform with the geometry of the existing roof. Model the size and shape of the new ducts so that the impact on the roofscape is minimised. Finish the new ducts in a non-reflective material that is neutral in colour and mid-tone. | High |
| 19.002 | Chimney | | High | Repair and retain | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|---|------------|--------------|--|----------------|----------|
| 19.003 | Rainwater goods and other external services | | Adverse | Remove and make good wall surface. Replace defective and non-matching rainwater goods with cast iron fittings to match original. | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|----------------------------|------------|--------------|---|----------------|----------|
| 19.004 | External stone wall facing | | High | Carry out close inspection of painted areas to determine extent of original granite facing and remove paint media where applicable. | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|-------------|------------|--------------|--|----------------|----------|
| 19.005 | Gun loops | | High | Remove concrete infilling and make good stonework where necessary. | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|-----------------|------------|--------------|--------------------------|----------------|---------|
| 19.006 | Look-out turret | | High | Repair and retain insitu | Not applicable | Neutral |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|-------------|------------|--------------|---|---|----------|
| 19.007 | Windows | | Moderate | Remove and make good stonework as necessary | Record existing windows on measured survey drawings | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|----------------------|------------|--------------|----------|----------------|----------|
| 19.008 | Modern partitions | | Adverse | Remove | Not applicable | Moderate |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|----------------------------------|--|--------------|----------|----------------|----------|
| 19.009 | Electrical services | A SERVICE OF THE PROPERTY OF T | Adverse | Remove | Not applicable | Moderate |
| 19.010 | Lay-in grid suspended ceiling | | Adverse | Remove | Not applicable | High |

| Element no. | Description | Photo ref. | Significance | Proposal | Mitigation | Impact |
|----------------|-------------------------------|------------|--------------|--------------------------|-------------------------------------|---------|
| 19.011 | Exposed timber roof structure | | High | Repair and retain insitu | Not applicable | Neutral |
| 19.012 | Timber stair | | Moderate | Remove | Record on measured surveys drawings | Low |
