

CONTRACT NO: HK/2015/01

WANCHAI DEVELOPMENT PHASE II AND CENTRAL WANCHAI BYPASS SAMPLING, FIELD MEASUREMENT AND TESTING WORK (STAGE 3)

ENVIRONMENTAL PERMIT NO. EP-364/2009/E, FURTHER EVIRONMENTAL PERMIT NOS. FEP-01/364/2009, FEP-02/364/2009, FEP-05/364/2009/A, FEP-07/364/2009/D, FEP-09/364/2009/B, FEP-10/364/2009/B AND FEP-11/364/2009/E, FEP-12/364/2009/D

MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT

- SEPTEMBER 2018 -

CLIENTS:

Civil Engineering and Development Department

and

Highways Department

PREPARED BY:

Lam Geotechnics Limited

11/F Centre Point 181-185 Gloucester Road, Wanchai, H.K.

Telephone: (852) 2882-3939 Facsimile: (852) 2882-3331 E-mail: <u>info@lamenviro.com</u> Website: <u>http://www.lamenviro.com</u>

CERTIFIED BY:

Raymond Dai Environmental Team Leader

DATE:

11 October 2018



Ref.: AACWBIECEM00_0_10779L.18

12 October 2018

By Post and Fax (2691 2649)

AECOM Asia Company Limited 11/F, Tower 2 Grand Central Plaza 138 Shatin Rural Committee Road Shatin, New Territories Hong Kong

Attention: Mr. Conrad Ng

Dear Mr. Ng,

Re: Contract No. HK/2015/01

Wan Chai Development Phase II - Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

Monthly Environmental Monitoring and Audit Report (September 2018) for EP-364/2009/E, FEP-01/364/2009, FEP-02/364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A, FEP-07/364/2009/D, FEP-09/364/2009/B, FEP-10/364/2009/B, FEP-11/364/2009/E and FEP-12/364/2009/D

Reference is made to the Environmental Team's submission of the captioned Monthly Environmental Monitoring and Audit (EM&A) Report for September 2018 received by e-mail on 11 October 2018 for our review and comment.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 in the captioned Environmental Permits.

Thank you very much for your attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,

David Yeung Independent Environmental Checker

c.c.	HyD	Attn: Mr. Tony Cheung	by fax: 2714 5289
	CEDD	Attn: Mr. Henry Tsang	by fax: 2301 1277
	Lam	Attn: Mr. Raymond Dai	by fax: 2882 3331
	AECOM	Attn: Mr. Francis Leong/ Stephen Lai	by fax: 2691 2649

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00_0_10779L.18.docx



TABLE OF CONTENTS

Lam Geotechnics Limited

EX	ECUTI	IVE SUMMARY	4
1	INTR	ODUCTION	10
	1.1 1.2	Scope of the Report Structure of the Report	
2	PROJ	ECT BACKGROUND	12
	2.1 2.2 2.3 2.4	Background Scope of the Project and Site Description Division of the Project Responsibility Project Organization and Contact Personnel	13 14
3	STAT	US OF REGULATORY COMPLIANCE	21
	3.1	Status of Environmental Licensing and Permitting under the Project	21
4	MON	ITORING REQUIREMENTS	33
	4.1 4.2	Noise Monitoring Air Quality Monitoring	
5	MON	TORING RESULTS	37
	5.1 5.2 5.3 5.4	Noise Monitoring Results Real Time Noise Monitoring Results Air Quality Monitoring Results Waste Monitoring Results	41 43
6	COM	PLIANCE AUDIT	52
	6.1 6.2 6.3 6.4	Noise Monitoring Air Quality Monitoring Review of the Reasons for and the Implications of Non-compliance Summary of action taken in the event of and follow-up on non-compliance	53 53
7		ULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT ECTS	53
8	ENVI	ROMENTAL SITE AUDIT	55
9	СОМ	PLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION	57
10	CON	CLUSION	59



LIST OF TA	ABLES
Table 2.1	Schedule 2 Designated Projects under this Project
Table 2.2	Details of Individual Contracts under the Project
Table 2.3	Contact Details of Key Personnel
Table 3.1	Summary of the current status on licences and/or permits on environmental
	protection pertinent to the Project
Table 3.2	Cumulative Summary of Valid Licences and Permits under Contract no.
	HK/2009/01
Table 3.3	Summary of submission status under FEP-02/364/2009
Table 3.4	Cumulative Summary of Valid Licences and Permits under Contract no.
	HK/2009/02
Table 3.5	Summary of submission status under FEP-01/364/2009
Table 3.6	Cumulative Summary of Valid Licences and Permits under Contract no.
	HY/2009/18
Table 3.7	Summary of submission status under FEP-05/364/2009/A
Table 3.8	Cumulative Summary of Valid Licences and Permits under Contract no.
	HY/2009/15
Table 3.9	Summary of submission status under FEP-06/364/2009/A
Table 3.10	Cumulative Summary of Valid License and Permits under Contract no. HY/2009/19
Table 3.11	Summary of submission status under FEP-07/364/2009/D
Table 3.12	Cumulative Summary of Valid License and Permits under Contract no. HK/2012/08
Table 3.13	Summary of submission status under FEP-12/364/2009/D
Table 3.14 Table 3.15	Cumulative Summary of Valid License and Permits under Contract no. HY/2010/08 Summary of submission status under FEP-10/364/2009/B
Table 3.15	Cumulative Summary of Valid License and Permits under Contract no. HY/2011/08
Table 3.10	Summary of submission status under FEP-11/364/2009/E
Table 3.17 Table 4.1	Noise Monitoring Stations
Table 4.1 Table 4.2	Real Time Noise Monitoring Stations
Table 4.2	Air Quality Monitoring Stations
Table 5.1	Noise Monitoring Stations for Contract no. HY/2009/18 (NOT USED)
Table 5.2	Noise Monitoring Station for Contract no HK/2009/01 and HK/2009/02
Table 5.3	Noise Monitoring Stations for Contract no. HY/2009/15
Table 5.4	Noise Monitoring Stations for Contract no. HY/2009/19
Table 5.5	Noise Monitoring Stations for Contract no. HY/2010/08
Table 5.6	Noise Monitoring Stations for Contract no. HY/2011/08
Table 5.7	Real Time Noise Monitoring Stations for Contract no. HY/2009/19
Table 5.8	Real Time Noise Monitoring Stations for Contract no. HY/2011/08
Table 5.9	Air Quality Monitoring Station for Contract no. HY/2009/18 (NOT USED)
Table 5.10	Air Quality Monitoring Station for Contract no. HK/2009/01(NOT USED)
Table 5.11	Air Quality Monitoring Station for Contract no. HK/2009/02
Table 5.12	Air Quality Monitoring Stations for Contract no. HY/2009/15(NOT USED)
Table 5.13	Air Quality Monitoring Station for Contract no. HY/2009/19
Table 5.14	Air Quality Monitoring Station for Contract no. HK/2012/08
Table 5.15	Air Quality Monitoring Stations for Contract no. HY/2010/08
Table 5.16	Air Quality Monitoring Stations for Contract no. HY/2011/08
Table 5.17	Details of Waste Disposal for Contract no. HK/2009/01(NOT USED)
Table 5.18	Details of Waste Disposal for Contract no. HK/2009/02
Table 5.19	Details of Waste Disposal for Contract no. HY/2009/18
Table 5.20	Details of Waste Disposal for Contract no. HY/2009/15
Table 5.21	Details of Waste Disposal for Contract no. HY/2009/19
Table 5.22	Details of Waste Disposal for Contract no. HK/2012/08
Table 5.23	Details of Waste Disposal for Contract no. HY/2010/08
Table 5.24	Details of Waste Disposal for Contract no. HY/2011/08
Table 8.1	Summary of Environmental Inspections for Contract no. HY/2009/15 (NOT USED)
Table 8.2	Summary of Environmental Inspections for Contract no. HY/2009/18 (NOT USED)
Table 8.3	Summary of Environmental Inspections for Contract no. HY/2009/19
<i>Table 8.4</i> <i>Table 8.5</i>	Summary of Environmental Inspections for Contract no. HK/2009/01 (NOT USED) Summary of Environmental Inspections for Contract no. HK/2009/02
	Caninary of Environmental inspections for Contract no. Inv2003/02



- Lam Geotechnics Limited
- Table 8.6
 Summary of Environmental Inspections for Contract no. HK/2012/08
- Table 8.7 Summary of Environmental Inspections for Contract no. HY/2010/08
- Table 8.8
 Summary of Environmental Inspections for Contract no. HY/2011/08)NOT USED)
- Table 9.1
 Cumulative Statistics on Complaints
- Table 9.2
 Cumulative Statistics on Successful Prosecutions
- Table 10.1
 Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting period

LIST OF FIGUREs

- Figure 2.1 Project Layout
- Figure 2.2 Project Organization Chart
- Figure 4.1 Locations of Environmental Monitoring Stations

LIST OF APPENDICES

- Appendix 3.1 Environmental Mitigation Implementation Schedule
- Appendix 4.1 Action and Limit Level
- Appendix 4.2 Copies of Calibration Certificates
- <u>Appendix 5.1</u> Monitoring Schedule for Reporting period and Coming month
- Appendix 5.2 Noise Monitoring Results and Graphical Presentations
- Appendix 5.3 Air Quality Monitoring Results and Graphical Presentations
- <u>Appendix 5.4</u> Real-time Noise Monitoring Results and Graphical Presentations
- Appendix 6.1 Event Action Plans
- Appendix 6.2 Notification of Exceedance
- Appendix 9.1 Complaint Log
- Appendix 10.1 Construction Programme of Individual Contracts



EXECUTIVE SUMMARY

- This is the Environmental Monitoring and Audit (EM&A) Monthly Report September 2018 specific for Environmental Permit no. EP-364/2009/E, Further Environmental Permit nos. FEP-01/364/2009, FEP-02-364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A FEP-07/364/2009/D, FEP-09/364/2009/B, FEP-10/364/2009/B, FEP-11/364/2009/E and FEP-12/364/2009/D. The EM&A report is prepared by the Environmental Team (ET) employed under Contract No. HK/2015/01 Wan Chai Development Phase II and Central Wanchai Bypass Sampling, Field Measurement and Testing Works (Stage 3). This report presents the environmental monitoring findings and information recorded during the period of 27 August 2018 to 26 September 2018.
- ii. The implementation of the Environmental Monitoring and Audit Programme for the Wan Chai Development phase II and Central-Wan Chai Bypass Project has been taken over by the Lam Geotechnics Limited (LGL) under Contract HK/2015/01 – Wan Chai Development Phase II and Central Wanchai Bypass – Sampling, Field Measurement and Testing Works (Stage 3) from 27 December 2015 in continuation of the previous Environmental Team employed under Contact HK/2011/07 – Wan Chai Development Phase II and Central Wanchai Bypass – Sampling, Field Measurement and Testing Works (Stage 2).
- iii. In the reporting period, the principal work activities of individual contracts are included as follows:

<u>Contract no. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at</u> <u>Wan Chai East (CWB Tunnel) under FEP-01/364/2009</u>

- New PMMA for the replacement of 8 nos. of damaged PMMA panels
- Drainage work
- Backfilling behind seawall block
- Removal of temporary reclamation of TWCR4
- Saw cutting of Northern D-Wall
- Pipe piling works for Box Culvert O Bay 12 and construction of DN1200 pipe
- Drainage connection works for Box Culvert O
- Demolition of existing Box Culvert O Bay 12
- Construction of earthing platform for pipe piling works at Box Culvert O Bay 12
- Fabrication of seawall blocks
- Backfilling and road works for Hung Hing Road at-grade Road
- Temporary drainage system for stock piling at Portion 5
- DN600 sewerage works across Hung Hing Road
- Remedial works for covered walkway at Expo Drive East

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

- Approach ramp structure, drainage and noise enclosure construction works
- Bridge noise enclosure installation works
- FEHD depot re-provision works
- Oil street drainage works



- Watson Road Watermains laying works
- Hing Fat Street road and drainage works
- Trough B & C construction.
- SR13 drainage works.
- Seawall block reinstatement near box culvert T1

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West under FEP-12/364/2009/D</u>

- Construction of Slip Road 1
- Construction of drainage
- Construction of roundabout

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009/B

- Tree replanting works in VP
- Drainage improvement works
- Utility diversion works
- Retaining wall works
- Junction modification

<u>Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems</u> and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E

- Construction of Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building
- Application of road marking inside tunnel, asphalt pavement
- Installation of Electricals and Mechanicals
- Installation of Tunnel Features
- Man Po Street widening works
- Traffic sign installation and modification of directional sign at various locations



Noise Monitoring

- iv. Noise monitoring during daytime was conducted at M1a Footbridge for Harbour Road Sports Center; M2b - Noon-day gun area; M3a - Tung Lo Wan Fire Station; M4b - Victoria Center; M5b - City Garden, M6 - HK Baptist Church Henrietta Secondary School, M7e and M7w – International Financial Centre East Podium and International Finance Centre West Podium and M8 – City Hall on weekly basis in the reporting period.
- With respect to the shift in major construction site portions at Wan Chai North, the noise monitoring station M1a – Harbour Road Sports Centre was finely adjusted from East of Harbour Road Sports Centre to West of Harbour Road Sports Centre on 21 June 2016.
- vi. With respect to the demolition of Ex-Harbour Road Sports Centre, the respective noise monitoring station M1a Harbour Road Sports Centre were finely adjusted on 16 and 25 May 2017 and thereafter to the Footbridge for Harbour Road Sports for noise monitoring.
- vii. With respect to the non-CWB Project building construction at Oil Street, the real-time noise monitoring station RTN2a- Hong Kong Electric Centre was finely adjusted from Northeast Side to Northwestern side at Roof Top location on 03 March 2017.
- viii. No action or limit level exceedance was recorded in the reporting period.
- ix. 24-hour real time noise monitoring was conducted at RTN1 FEHD Hong Kong Transport Section Whitfield Depot. No limit level exceedance was recorded in the reporting period.
- x. 24-hour real time noise monitoring was conducted at RTN2a Hong Kong Electric Centre. No limit level exceedance was recorded in the reporting period.
- xi. 24-hour real time noise monitoring was conducted at RTN3 Yu Lee Mo Fan Memorial School. Limit level exceedance was recorded on 13 September 2018 during the monitoring period. After the investigation, the exceedance was concluded as non-project related.
- xii. 24-hour real time noise monitoring was conducted at RTN4 Causeway Bay Community Centre. No limit level exceedance was recorded in the reporting period.

Air Quality Monitoring

- xiii. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted at CMA1b – Harbour Grand Hotel Boundary Wall; CMA2a - Causeway Bay Community Center; CMA3a - CWB PRE Site Office Area; CMA4a – Society for the Prevention of Cruelty to Animals; CMA5b - Pedestrian Plaza; MA1e and MA1w – International Finance Centre eastern and western podium on every six days basis.
- xiv. No action or limit level exceedance was recorded in the reporting period.
- xv. With respect to the proposed demolition of eastern podium of Oil Street Site Office, the respective air quality monitoring station CMA1b – Oil Street Site Office was finely adjusted from East podium of the Oil Street Site Office to the West podium of the Oil Street Site Office on 21 December 2016.
- with respect to the proposed demolition of the Oil Street Site Office, the respective air quality monitoring station CMA1b Harbour Grand Hotel Boundary Wall was finely adjusted from the Oil Street Site Office to Harbor Grand Hotel Boundary Wall from 05 June 2017 onwards.
- xvii. No action or limit level exceedance was recorded in the reporting period.
- Complaints, Notifications of Summons and Successful Prosecutions
- Xviii. One environmental complaint and summons was received in the reporting period.
 An EPD complaint was referred to the ET on 3 September 2018 (CASE Ref: H08/RS/00024048-18). The complainant reported that: Night time construction noise on



Island Eastern Corridor outside Provident Centre at around 1:00 a.m. on 31st August, 2018. ET confirmed with the Resident Site Staff that 1) There was no construction activity undertaken by Contract HY/2011/08 at Island Eastern Corridor during the restricted hours from 2300hrs on 30 August 2018 to 0700hrs on 31 August 2018. 2) The Contractor of HY/2009/19 reported that paving work was conducted during the period of 0100hrs to 0600hrs at 31 August 2018 at the works area from D12 to F8 where was located inside the noise semi-enclosure of IEC. Total 4 nos. dump truck, 1 nos. paver, 1 no. vibratory roller and 1no. road roller with QPME label were used for the paving work.

Relevant Construction Noise Permit GW-RS0679-18 was in place for the construction works conducted during the above concerned periods. The PMEs operated during the concerned period was included in Construction Noise Permit GW-RS0679-18 Condition 3.a. Group F. Based on RSS information, the noise control measure listed in Construction Noise Permit GW-RS0679-18 Condition 3.d.9 including installation of engine exhaust silencers for asphalt paver and installation of absorbing lining to the engine compartment for road roller and vibratory roller were generally in place. Meanwhile, there is no sufficient information to conclude if the concerned asphalt paver installed with absorbing lining to the engine compartment; and concerned road roller and vibratory roller installed with engine exhaust silencers according to Construction Noise Permit GW-RS0679-18 Condition 3.d.9.

In view of the above, the Contractor of HY/2009/19 was advised to critically check and confirm the noise control measures listed in Construction Noise Permit GW-RS0679-18 Condition 3.d.9 for concerned PMEs to ensure the operation of PMEs shall strictly follow the construction noise permit condition. The Contractor of HY/2009/19 was also reminded to maintain regular checking and maintenance of the PMEs and it's noise control measures deployed to avoid potential nuisance to the nearby public. Site Inspections and Audit

- xix. The Environmental Team (ET) conducted weekly site inspections for Contract no. HY/2009/19, HY/2010/08, HK/2009/02, HK/2012/08 and HY/2011/08 in this reporting period.
 - xx. Construction of bored pile E3B under HY/2009/17 was confirmed completed and the respective work area under FEP-03/364/2009 was handover and inspected under HY/2009/19 from 19 Dec 2012 onwards.
 - xxi. Construction works under HK/2010/06 was confirmed completed and the respective work area under FEP-08/364/2009/A was handover and inspected under HK/2012/08 from 22 Sep 2014 onwards.
 - xxii. As confirmed with CWB RSS, the construction works under Contract HY/2009/15 was completed from 27 October 2017 onwards. The respective weekly site audit inspection for HY/2009/15 was therefore suspended from 27 October 2017 onwards.
 - xxiii. The Contractors rectified major observations and recommendations made during the audit sessions. No non-conformance was identified during the site inspections.
 - xxiv. As confirmed with CWB RSS, the construction works under Contract HY/2009/18 was completed from 25 April 2018 onward. The respective weekly site audit inspection for HY/2009/18 was therefore temporary suspended from 27 April 2018 onwards.
 - xxv. As confirmed with WDII RSS and with respect to the joint inspection conducted with IEC on 25 May 2018, RSS, ET and IEC share the view that there is no adverse environmental impact of remaining works under Contract HK/2009/01 and the respective environmental site inspection was temporary suspended from 26 May 2018 onwards.



Future Key Issues

i. In the coming reporting period, the principal work activities of individual contracts are anticipated as follows:

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East (CWB Tunnel) under FEP-01/364/2009</u>

- Rectification work for the replacement of 8 nos. of damaged PMMA panels
- Drainage work
- Removal of TWCR4
- Saw cutting and removal of Northern D-wall for Portion 3&4
- Construction of seawall coping at Portion 3&4
- Backfilling works behind seawall blocks and adjacent Box Culvert O.
- Construction of drainage system for Box Culvert O and Hung Hing Road at-grade Road
- Fabrication of seawall block
- Temporary works for construction of Box Culvert O Bay 12
- Stockpiling and internal transfer of excavated materials from Portions 3&4.
- Monitoring and maintain temporary drainage system for stockpiling.
- Rectification works for damaged CMS cover under C1
- Rectification of CMS termination box cover.
- DN600 sewerage works across Hung Hing Road.
- Remedial works for covered walkway at Expo Drive East

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

- Approach ramp structure, drainage and noise enclosure construction works
- Bridge noise enclosure installation works
- FEHD re-provision works
- Oil Street drainage works
- Watson Road Watermains laying works
- Hing Fat Street road and drainage works
- Trough B & C construction
- SR13 drainage works
- Seawall block reinstatement near box culvert T1
- Landscape deck soft landscaping works

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West under FEP-12/364/2009/D</u>

- Construction of Slip Road 1
- Construction of drainage
- Construction of roundabout



Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009

- Tree replanting works in VP
- Drainage improvement works
- Utility diversion works
- Retaining wall works
- Junction modification

<u>Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems</u> and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E

- ABWF works at Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building
- Construction works at SCB and SCP area
- Application of road marking inside the Tunnel, asphalt pavement
- Installation and testing of Electricals and Mechanicals
- Installation of Tunnel Features
- Man Po Street widening works
- Traffic sign installation and modification of directional sign at various locations



1 INTRODUCTION

1.1 Scope of the Report

- 1.1.1. Lam Geotechnics Limited (LGL) has been appointed to work as the Environmental Team (ET) under Environmental Permit no. EP-364/2009/E and Further Environmental permit nos. FEP-01/364/2009, FEP-02-364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A FEP-07/364/2009/D, FEP-09/364/2009/B, FEP-10/364/2009/B, FEP-11/364/2009/E and FEP-12/364/2009/D to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) and in the EM&A Manual of the approved EIA Report for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001).
- 1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 10.3 of EM&A Manual and "*Environmental Monitoring and Audit Requirements*" under Particular Specification Section 27.
- 1.1.3. This report documents the finding of EM&A works for Environmental Permit (EP) no. EP-364/2009/E, Further Environmental Permit (FEP) nos. FEP-01/364/2009, FEP-02-364/2009, FEP-05/364/2009/A, FEP-06/364/2009/A FEP-07/364/2009/D, FEP-09/364/2009/B, FEP-10/364/2009/B, FEP-11/364/2009/E and FEP-12/364/2009/D during the period 27 August 2018 to 26 September 2018.

1.2 Structure of the Report

- **Section 1** *Introduction* details the scope and structure of the report.
- Section 2 *Project Background* summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3 Status of Regulatory Compliance summarizes the status of valid Environmental Permits / Licenses during the reporting period.
- Section 4 *Monitoring Requirements* summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.
- **Section 5** *Monitoring Results* summarizes the monitoring results obtained in the reporting period.
- **Section 6 Compliance Audit** summarizes the auditing of monitoring results, all exceedances environmental parameters.



- Section 7 *Cumulative Construction Impact due to the Concurrent Projects* summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.
- **Section 8** *Environmental Site Audit* summarizes the findings of weekly site inspections undertaken within the reporting period, with a review of any relevant follow-up actions within the reporting period.
- Section 9 Complaints, Notification of summons and Prosecution summarizes the cumulative statistics on complaints, notification of summons and prosecution
- Section 10 Conclusion



2 PROJECT BACKGROUND

2.1 Background

- 2.1.1. "Wan Chai Development phase II and Central-Wan Chai Bypass" and "Central-Wan Chai Bypass and Island Eastern Corridor Link" (hereafter called "the Project") are Designated Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001) and Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) have been approved on 31 August 2001 and 11 December 2008 respectively.
- 2.1.2. The key purpose of Wan Chai Development Phase II (WDII) is to provide land at Wan Chai North and North Point for construction of the Central-Wan Chai Bypass and Island Eastern Corridor Link (CWB). Land formed under the project will be developed as a world-class waterfront promenade joining that at the new Central waterfront for public enjoyment.
- 2.1.3. There is a compelling and present need for the CWB to provide relief to the very congested east-west Connaught Road Central/Harcourt Road / Gloucester Road Corridor (the Corridor) which is currently operating beyond its capacity. The CWB will provide relief to the existing congestion along the Corridor and cater for the anticipated growth of traffic on Hong Kong Island. Without the CWB and its access roads, there will not be sufficient capacity to serve the heavy traffic demands at both strategic and local levels.



2.2 Scope of the Project and Site Description

- 2.2.1. Design and Construction of Central Wan Chai Bypass and Island Eastern Corridor Link under the Project involves the construction and operation of a trunk road and its road tunnel more than 800m in length between portals that is shown at *Figure 2.1*.
- 2.2.2. The study area encompasses existing developments from Central to North Point. The scope of the Central-Wanchai Bypass (CWB) and Island Eastern Corridor Link (IECL) includes:
 - A dual three-lane trunk road, approximately 4.5 km in length, and tunnel approximately 3.7 km in length defined from the connection with the existing Rumsey Street Flyover in Central, through to a connection with the existing Island Eastern Corridor to the east of the Causeway Bay Typhoon Shelter (CBTS);
 - The Central Interchange near the Rumsey Street Flyover to provide road connections to the Central area;
 - Tunnel control buildings and ventilation buildings;
 - Slip roads to connect the CWB to the local road system in the Wan Chai North and Causeway Bay area;
 - Associated road lighting, road signing, traffic control and surveillance system; and
 - Other associated works.
- 2.2.3. The project also contains various Schedule 2 DPs that, under the EIAO, require Environmental Permits (EPs) to be granted by the DEP before they may be either constructed or operated. *Table 2.1* summarises the five individual DPs under this Project. *Figure 2.1* shows the locations of these Schedule 2 DPs.

Item	Designated Project	EIAO Reference	Reason for inclusion
DP1	Central-Wanchai Bypass (CWB) including its road tunnel and slip roads	Schedule 2, Part I, A.1 and A.7	Trunk road and road tunnel more than 800 m in length
DP2	Road P2 and other roads which are classified as primary/district distributor roads	Schedule 2, Part I, A.1	Primary / district distributor roads
DP3	Reclamation works including associated dredging works	Schedule 2, Part I, C.1 and C.12	Reclamation more than 5 ha in size and a dredging operation less than 100 m from a seawater intake point
DP5	Wan Chai East Sewage Outfall	Schedule 2, Part I, F.5 and F.6	Submarine sewage pipelines with a total diameter more than 1,200 mm and include a submarine sewage outfall
DP6	Dredging for the Cross- harbour Water Mains from Wan Chai to Tsim Sha Tsui	Schedule 2, Part I, C.12	A dredging operation less than 100 m from a seawater intake point

 Table 2.1
 Schedule 2 Designated Projects under this Project



2.3 Division of the Project Responsibility

2.3.1. Due to the multi-contract nature of the Project, there are a number of contracts sub-dividing the whole works area into different work areas to be commenced. Contractors of individual contracts will be required by the EP holder to apply Further Environmental Permits such that the impact monitoring stations are sub-divided accordingly to facilitate the implementation of EM&A programme and to streamline the EM&A reporting for individual FEP holders correspondingly.

2.3.2. The details of individual contracts are summarized in *Table2.2*.

Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
HY/2009/17	Central – Wan Chai Bypass (CWB) at	DP1	5 October 2010
	FEHD Whitfield Depot – Advanced piling works.		(Completed)
HY/2009/18	Central – Wan Chai Bypass (CWB) –	DP1	21 April 2011
	Central Interchange		(Completed)
04/HY/2006	Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street	DP1	September 2010 (Completed)
HK/2009/01	Wan Chai Development Phase II -	DP1, DP2	25 August 2011
	Central – Wan Chai Bypass at Hong Kong Convention and Exhibition Centre – Tunnel Works		(Completed)
HK/2009/02	Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East(CWB Tunnel)	DP1	26 April 2011
HY/2009/15	Central-Wanchai Bypass – Tunnel	DP1,DP3	13 July 2011
	(Causeway Bay Typhoon Shelter Section)		(Completed)
HY/2009/19	Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link	DP1	24 March 2011
HK/2010/06	Wan Chai Development Phase II-	DP3	22 March 2011
	Central-Wan Chai Bypass over MTR Tsuen Wan Line		(Completed)
HK/2012/08	Wan Chai Development Phase II- Central-Wan Chai Bypass at Wan Chai West	DP1,DP2, DP3	10 March 2014
HY/2010/08	Central- Wanchai Bypass Tunnel – Tunnel (Slip Road 8)	DP1, DP2, DP3	21 March 2013
HY/2011/08	Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning	DP1	8 October 2014

Table 2.2 Details of Individual Contracts under the Project



2.4 Project Organization and Contact Personnel

- 2.4.1. Civil Engineering and Development Department and Highways Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.4.2. The proposed project organization and lines of communication with respect to environmental protection works are shown in *Figure 2.2*. Key personnel and contact particulars are summarized in *Table 2.3*:

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Chief Resident Engineer	Ms. Gloria Tang	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3912 3388	3912 3328
Chun Wo – CRGL Joint	Contractor under Contract	Project Manager	Mr. Paul Yu	3658 3085	2827 9996
Venture	no. HK/2009/02	Environmental Officer	Mr. C.P. Ho	9191 8856	
Chun Wo -	Contractor	Project Manager	Mr. David Lau	3758 8879	
CRGL - MBEC_Joint	under Contract no. HY/2009/19	Site Agent	Mr. William Luk	9456 9819]
Venture		Deputy Site Agent	Mr. Andy Chan	3758 8879	
		Environmental Officer	Mr. M.H. Isa	3757 8218	
		Assistant Environmental Officer	Mr. James Chan	3757 8217	2570 8013
		Construction Manager (Marine)	Mr. Wingo Wong	9300 2625	
		Construction Manager (Land)	Mr. Mark Mak	9356 4421	
		Construction Manager (Land)	Mr. Yung Kwok Wah	9834 1010	
Leighton	Contractor	Site Agent	Mr. Jimmy Chu	3973 0803	2140 6799
Contractors (Asia) Limited	under Contract no. HY/2009/18	Construction Manager	Mr. Darren Grant	3971 1460	
		Environmental Supervisor	Ms. Penny Yiu	3973 1065	
China State	Contractor	Project Director	Mr. Chris Leung	3557 6393	2865 5229
Construction	under Contract	Site Agent	Mr. Patrick Ho	3557 6405	2566 2192

Table 2.3 Contact Details of Key Personnel



Party	Role	Post	Name	Contact No.	Contact Fax
Engineering (HK) Ltd.	no. HY/2009/15	Environmental Officer	Mr. Desmond Ho	3557 6347	
China State-	Contractor	Project Director	Mr. C.N. Lai	9137 1811	2877 1522
Build King JV	under Contract no. HK/2012/08	Site Agent	Mr. George Cheung	9268 1918	
		Environmental Officer	Mr. James MA	9130 9549	
		Environmental Supervisor	Mr. Y. L. Ho	9856 5669	
China State	Contractor	Project Director	Chris Leung	9210 7116	2566 8061
	under Contract no. HY/2010/08	Site Agent	Mr. Thomas Lui	3557 6407	
		Environmental Officer	Mr. Gabriel Wong	3557 6466	
Leighton Joint Venture	Contractor under Contract	Site Agent	Mr. Colman Wong	2823 1410	21406799
	no. HY/2011/08	Environmental Officer	Ms. Penny Yiu	3973 1065	
Ramboll Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechnics Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331



2.4.3. In this reporting period, the principal work activities of individual contracts are included as follows:

<u>Contract no. HK/2009/02 - Wan Chai Development Phase II - Central - Wan Chai Bypass at</u> <u>Wan Chai East (CWB Tunnel) under FEP-01/364/2009</u>

- New PMMA for the replacement of 8 nos. of damaged PMMA panels
- Drainage work
- Backfilling behind seawall block
- Removal of temporary reclamation of TWCR4
- Saw cutting of Northern D-Wall
- Pipe piling works for Box Culvert O Bay 12 and construction of DN1200 pipe
- Drainage connection works for Box Culvert O
- Demolition of existing Box Culvert O Bay 12
- Construction of earthing platform for pipe piling works at Box Culvert O Bay 12
- Fabrication of seawall blocks
- Backfilling and road works for Hung Hing Road at-grade Road
- Temporary drainage system for stock piling at Portion 5
- DN600 sewerage works across Hung Hing Road
- Remedial works for covered walkway at Expo Drive East

Contract no. HY/2009/19 - Central - Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

- Approach ramp structure, drainage and noise enclosure construction works
- Bridge noise enclosure installation works
- FEHD depot re-provision works
- Oil street drainage works
- Watson Road Watermains laying works
- Hing Fat Street road and drainage works
- Trough B & C construction.
- SR13 road & drainage works.
- Seawall block reinstatement near box culvert T1.

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West under FEP-12/364/2009/D</u>

- Construction of Slip Road 1
- Construction of drainage
- Construction of roundabout

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009/B

- Tree replanting works in VP
- Drainage improvement works
- Utility diversion works
- Retaining wall works
- Junction modification

<u>Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems</u> and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E

- Construction of Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building
- Application of road marking inside the Tunnel, asphalt pavement
- Installation of Electricals and Mechanicals
- Installation of Tunnel Features

Lam Geotechnics Limited

- Man Po Street widening works
- Traffic sign installation and modification of directional sign at various locations



2.4.4. In coming reporting period, the principal work activities of individual contracts are anticipated as follows:

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass</u> <u>at Wan Chai East (CWB Tunnel) under FEP-01/364/2009</u>

- Rectification work for the replacement of 8 nos. of damaged PMMA panels
- Drainage work
- Removal of TWCR4
- Saw cutting and removal of Northern D-wall for Portion 3&4.
- Construction of seawall coping at Portion 3&4.
- Backfilling works behind seawall blocks and adjacent Box Culvert O.
- Construction of drainage system for Box Culvert O and Hung Hing Road at-grade Road.
- Fabrication of seawall block
- Temporary works for construction of Box Culvert O Bay 12
- Stockpiling and internal transfer of excavated materials from Portions 3&4.
- Monitoring and maintain temporary drainage system for stockpiling.
- Rectification works for damaged CMS cover under C1.
- Rectification of CMS termination box cover.
- DN600 sewerage works across Hung Hing Road.
- Remedial works for covered walkway at Expo Drive East

<u>Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and</u> <u>Island Eastern Corridor Link under FEP-07/364/2009/D</u>

- Approach ramp structure, drainage and noise enclosure construction works
- Bridge noise enclosure installation works
- FEHD re-provision works
- Oil Street drainage works
- Watson Road Watermains laying works
- Hing Fat Street road and drainage works
- Trough B & C construction
- SR13 drainage works
- Seawall block reinstatement near box culvert T1
- Landscape deck soft landscaping works

<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West under FEP-12/364/2009/D</u>

- Construction of Slip Road 1
- Construction of drainage
- Construction of roundabout



Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8) under FEP-10/364/2009

- Tree replanting works in VP
- Drainage improvement works
- Utility diversion works
- Retaining wall works
- Junction modification

<u>Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems</u> and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E

- ABWF works at Ventilation Buildings, inclusive of Administration Building, Central Ventilation Building, East Ventilation Shaft/Building, West Ventilation Building
- Construction works at SCB and SCP area
- Application of road marking inside the Tunnel, asphalt pavement
- Installation and testing of Electricals and Mechanicals
- Installation of Tunnel Features
- Man Po Street widening works
- Traffic sign installation and modification of directional sign at various locations



3 STATUS OF REGULATORY COMPLIANCE

3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in *Table 3.1*.

Table 3.1	Summary of the current status on licences and/or permits on environmental
	protection pertinent to the Project

Permits and/or Licenses	Reference No.	Issued Date	Status
Environmental Permit	EP-356/2009	30 Jul 2009	Valid
Environmental Permit	EP-364/2009/E	22 Dec 2016	Valid
Environmental Permit	EP-376/2009	13 Nov 2010	Valid
Further Environmental Permit	FEP-01/356/2009	18 Feb 2010	Surrendered
Further Environmental Permit	FEP-02/356/2009	24 Mar 2010	Surrendered
Further Environmental Permit	FEP-03/356/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-04/356/2009	15 Nov 2010	Valid
Further Environmental Permit	FEP-05/356/2009	24 Mar 2011	Surrendered
Further Environmental Permit	FEP-06/356/2009	5 March 2013	Valid
Further Environmental Permit	FEP-07/356/2009	26 July 2013	Valid
Further Environmental Permit	FEP-01/364/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-02/364/2009	21 Apr 2010	Surrendered
Further Environmental Permit	FEP-03/364/2009	12 July 2010	Surrendered
Further Environmental Permit	FEP-04/364/2009/A	14 Oct 2010	Surrendered
Further Environmental Permit	FEP-05/364/2009/A	15 Nov 2010	Valid
Further Environmental Permit	FEP-06/364/2009/A	22 Nov 2010	Valid
Further Environmental Permit	FEP-07/364/2009/D	24 Nov 2015	Valid
Further Environmental Permit	FEP-08/364/2009/A	15 June 2012	Surrendered
Further Environmental Permit	FEP-09/364/2009/B	5 March 2013	Valid
Further Environmental Permit	FEP-10/364/2009/B	26 July 2013	Valid
Further Environmental Permit	FEP-11/364/2009/E	22 Dec 2016	Valid
Further Environmental Permit	FEP-12/364/2009/D	01 Aug 2016	Valid



3.1.2. Due to the multi-contract nature of the Project, the status of permits and/or licences under the individual contract(s) are presented as below:

<u>Contract no. HY/2009/17 – Central – Wan Chai Bypass (CWB) at FEHD Whitfield Depot –</u> <u>Advanced piling works under FEP-03/364/2009</u>

3.1.3. The construction works was completed and the FEP-03/364/2009 was surrendered by the Contractor on 28 March 2013.

<u>Contract no. 04/HY/2006 – Reconstruction of Bus Terminus near Man Yiu Street and Man</u> <u>Kwong Street under FEP-04/364/2009/A</u>

3.1.4. The construction works was completed, and the FEP-04/HY/2006 was surrendered by the Contractor on 11 February 2011.

<u>Contract no. HK/2010/06 - Wan Chai Development Phase II - Central - Wan Chai Bypass</u> over MTR Tsuen Wan Line under FEP-08/364/2009/A

3.1.5. The construction works was completed, and the FEP-08/364/2009/A was surrendered by the Contractor on 3 October 2014.

<u>Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon</u> <u>Shelter Section) under FEP-06/364/2009/A</u>

3.1.6. The Construction works under HY/2009/15 was confirm completed by the RSS from 27 October 2017 onwards. The weekly site audit inspection and the associated monitoring station for HY/2009/15 were temporary suspended from 27 October 2017 onwards.

<u>Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under</u> <u>FEP-05/364/2009/A</u>

3.1.7. The Construction works under HY/2009/18 was confirm completed by the RSS from 25 April 2018 onwards. The weekly site audit inspection and the associated monitoring station for HY/2009/18 were temporary suspended from 27 April 2018 onwards.

<u>Contract no. HK/2009/01 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Hong Kong Convention and Exhibition Centre – Tunnel Works under FEP-02/364/2009</u>

3.1.8. As confirmed with WDII RSS and with respect to the joint inspection conducted with IEC on 25 May 2018, RSS, ET and IEC share the view that there is no adverse environmental impact of remaining works under Contract HK/2009/01 and the respective environmental site inspection and associated monitoring station were temporary suspended from 26 May 2018 onwards. FEP-02/364/2009 was surrendered by the Contractor on 3 September 2018.



<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East (CWB Tunnel) under FEP-01/364/2009</u>

3.1.9. Summary of the current status on licences and/or permits on environmental protection pertinent and submission under FEP-01/364/2009 for contract no. HK/2009/02 are shown in *Table 3.4* and *Table 3.5.*

Table 3.4	Cumulative Summary of Valid Licences and Permits under Contract no.
	HK/2009/02

HK/2009/02				
Permits and/or Licenses	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental	FEP-03/356/2009	24 Mar 2010	N/A	Valid
Permit	FEP-01/364/2009	24 Mar 2010	N/A	Valid
Notification of Works Under APCO	313962	2 Feb 2010	N/A	Valid
Construction Noise	GW-RS0296-18	10 Apr 2018	23 Apr 2018 to 22 Oct 2018	Valid
Permit (CNP) for non-pilling	GW-RS0647-18	26 Jul 2018	28 Jul 2018 to 27 Jan 2019	Valid
equipment	GW-RS0674-18	31 Jul 2018	2 Aug 2018 to 31 Jan 2019	Valid
	GW-RS0713-18	14 Aug 2018	16 Aug 2018 to 14 Feb 2019	Valid
Water Discharge	WT00022295-2015	12 Aug 2015	31 July 2020	Valid
License	WT00025276-2016	19 Sep 2016	31 July 2021	Valid
Billing Account under Waste Disposal Ordinance (Land)	7010255	10 Feb 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance (Marine)	7011496	6 Oct 2010	N/A	Valid
Registration as Chemical Waste Producer (Wan Chai)	WPN5213-135- C3593-01	10 Mar 2010	N/A	Valid
Registration as Chemical Waste Producer (TKO 137)	WPN5213-839- C3593-02	22 Sep 2010	N/A	Valid



EP Condition	Submission	Date of Submission
Condition 2.7 and 2.8	ndition 2.7 and 2.8 Works Schedule and Location Plan	
Condition 2.6	Environmental Management Organization Chart	14 Jun 2011
Condition 1.12	Commencement Date of Works	21 Jun 2011
Condition 2.11	Landscape Plan (Revision B)	20 Nov 2012
Condition 2.9	Noise Management Plan (Revision B)	13 Jan 2012

Table 3.5 Summary of submission status under FEP-01/364/2009



<u>Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A</u>

3.1.10. Summary of the current status on licences and/or permits on environmental protection pertinent and submission under FEP-05/364/2009A for contract no. HY/2009/18 are shown in **Table 3.6** and **Table 3.7**.

Lam Geotechnics Limited

Table 3.6	Cumulative Summary of Valid Licences and Permits under Contract no.
	HY/2009/18

Permit / License / Notification / Approval	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-05/364/2009/A	15 Nov 2010	N/A	Valid
Notification of Works Under APCO	322293	07 Oct 2010	N/A	Valid
Construction Noise Permit (CNP) for non-piling equipment	-	-	-	-
Discharge Licenses	WT00024255-2016	18 May 2016	31 Jan 2021	Valid
Registration as a Chemical Waste Producer	WPN: 8335-121- L1048-04	17 Dec 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance (Land)	Account No.: 7011587	11 Oct 2010	N/A	Valid

Table 27	C	· of outputies is a status under FFD OF/264/2000/A
Table 3.7	Summar	of submission status under FEP-05/364/2009/A

EP Condition	Submission	Date of Submission
Condition 2.9	Noise Management Plan	01 March 2011
Condition 2.10	Final Landscape Plan (Rev. D2)	7 August 2018



<u>Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon</u> <u>Shelter Section) under FEP-06/364/2009/A</u>

3.1.11. Summary of the current status on licences and/or permits on environmental protection pertinent and submission under FEP-06/364/2009/A for contract no. HY/2009/15 are shown in *Table 3.8* and *Table 3.9.*

Table 3.8	Cumulative Summary of Valid Licences and Permits under Contract no.
	HY/2009/15

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further	FEP-06/364/2009/A	22 Nov 2010	N/A	Valid
Environmental Permit	FEP-04/356/2009	22 Nov 2010	N/A	Valid
Notification of Works Under APCO	321822	24 Sep 2010	N/A	Valid
Registration as a Chemical Waste Producer	WPN: 5213-147- C1169-35	15 Nov 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance	7011553	30 Sep 2010	N/A	Valid
Construction Noise Permit	N/A	N/A	N/A	N/A
Water Discharge License (Discharge at TS1)	WT00024874-2016	20 Jul 2016	20 Jul 2016 to 31 Mar 2021	Valid

Table 3.9	Summar	y of submission status under FEP-06/364/2009/A
	Summar	

EP Condition	Submission	Date of Submission
	Management Organization of Main Construction Companies	11 Mar 2011
Condition 2.6	Amendment for Management Organization of Main Construction Companies	16 May 2011
Condition 2.7	Works Schedule	15 Mar 2011
Condition 2.8	Location Plan	15 Mar 2011
Condition 2.9	Noise Management Plan	6 May 2011
Condition 2.10	Landscape Plan (Rev.5)	25 Jan 2018



Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

3.1.12. The current status on licences and/or permits on environmental protection pertinent and submission under FEP-07/364/2009/D for contract no. HY/2009/19 are shown in *Table 3.10* and *Table 3.11*.

Table 3.10 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/19

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-07/364/2009/D	24 Nov 2015	N/A	Valid
Notification of Works Under APCO	326160	24 Jan 2011	N/A	Valid
Registration as a Waste Producer	7012306	10 Feb 2011	N/A	Valid
Registration as Chemical Waste Producer	5213-151-C3654-01	24 Mar 2011	N/A	Valid
Application for Vessel Disposal	7013285	21 July 2011	N/A	Valid
	GW-RS0691-18	7 Aug 2018	10 Aug 2018 to 11 Nov 2018	Valid
Construction Noise	GW-RS0702-18	9 Aug 2018	12 Aug 2018 to 31 Oct 2018	Valid
Permits (CNP) for non- piling equipment	GW-RS0558-18	3 Jul 2018	6 Jul 2018 to 30 Sep 2018	Valid
	GW-RS0870-18	24 Sep 2018	26 Sep 2018 to 30 Nov 2018	Valid
Water Discharge License	WT00025282-2016	15 Sep 2016	30 Sep 2021	Valid

Table 3.11 Summary of submission status under FEP-07/364/2009/D

EP Condition	Submission	Date of Submission
Condition 2.13	Landscape Plan (Rev.6)	29 August 2017
Condition 2.9	Noise Management Plan (Rev.4)	07 December 2017



<u>Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at</u> <u>Wan Chai West under FEP-12/364/2009/D</u>

3.1.13. The current status on licences and/or permits on environmental protection pertinent and submission under FEP-12/364/2009/D for contract no. HK/2012/08 showed in *Table 3.12 and Table 3.13.*

HIV2012/00				
Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	FEP-09/364/2009/B	5 Mar 2013	N/A	Valid
Further Environmental Permit	FEP-12/364/2009/D	1 Aug 2016	N/A	Valid
	FEP-06/356/2009	05 Mar 2013	N/A	Valid
Notification of Works Under APCO	355439	4 Feb 2013	N/A	Valid
Registration as a Chemical Waste Producer	5213-134-C3790-01	30 Jun 2016	N/A	Valid
Billing Account under Waste Disposal Ordinance	7016883	18 Feb 2013	N/A	Valid
	GW-RS0732-18	17 Aug 2018	26 Aug 2018 to 25 Feb 2019	Valid
Construction Noise Permit (CNP) for non-piling equipment	GW-RS0597-17	10 Jul 2018	13 Jul 2018 to 12 Jan 2019	Valid
	GW-RS0513-18	7 Jun 2018	10 Jun 2018 to 4 Nov 2018	Valid
Water Discharge License	WT00020594-2014	22 Dec 2014	31 Jan 2019	Valid

 Table 3.12 Cumulative Summary of Valid Licences and Permits under Contract no.

 HK/2012/08

Table 3.13 Summary of submission status under FEP-12/364/2009/D

EP Condition	Submission	Date of Submission
Condition 2.9	Noise Management Plan (Rev.2)	9 July 2013
Condition 2.14	Landscape Plan (Rev.4)	24 August 2015



<u>Contract no. HY/2010/08 –Central – Wanchai Bypass Tunnel – Tunnel (Slip Road 8) under FEP-10/364/2009/B</u>

3.1.14. The current status on licences and/or permits on environmental protection pertinent and submission under FEP-10/364/2009/B for contract no. HK/2012/08 showed in *Table 3.14 and Table 3.15.*

Table 3.14	Cumulative Summary of Valid Licences and Permits under Contract no.
	HY/2010/08

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	FEP-10/364/2009/B	26 Jul 2013	NA	Valid
Further Environmental Permit	FEP-07/356/2009	26 Jul 2013	NA	Valid
Notification of Works Under APCO	357176	2 Apr 2013	NA	Valid
Registration as a Chemical Waste Producer	WPN5213-147- C1169-44	27 Mar 2013	NA	Valid
Billing Account under Waste Disposal Ordinance	7017170	27 Mar 2013	NA	Valid
Water Discharge Lipping	WT00031281-2018	31 Jul 2018	31 Jul 2023	Valid
Water Discharge License	WT00028744-2017	04 Aug 2017	31 Aug 2019	Valid
	GW-RS0812-18	7 Sep 2018	12 Sep 2018 to 10 Mar 2019	Valid
	GW-RS0307-18	18 Apr 2018	20 Apr 2018 to 17 Oct 2018	Valid
	GW-RS0374-18	8 May 2018	10 May 2018 to 9 Nov 2018	Valid
Construction Noise Permit (CNP)	GW-RS0446-18	1 June 2018	5 Jun 2018 to 4 Dec 2018	Valid
for non-piling equipment	GW-RS0556-18	28 June 2018	3 Jul 2018 to 24 Dec 2018	Valid
	GW-RS0701-18	7 Aug 2018	5 Aug 2018 to 31 Aug 2018	Expired
	GW-RS0744-18	22 Aug 2018	24 Aug 2018 to 30 Oct 2018	Valid
	GW-RS0813-18	7 Sep 2018	10 Sep 2018 to 5 Mar 2019	Valid



Table 3.15 Summary of submission status under FEP-10/364/2009/B

EP Condition	Submission	Date of Submission
Condition 2.9	Noise Management Plan (Rev.3)	03 January 2014
Condition 2.14	Landscape Plan (Rev.2)	19 May 2014
Condition 2.16	Additional Mitigation Plan (Rev.3)	31 August 2018

<u>Contract no. HY/2011/08 –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems</u> and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E

3.1.15. The current status on licenses and/or permits on environmental protection pertinent and submission under FEP-11/364/2009/E for contract no. HY/2011/08 showed in *Table 3.16 and Table 3.17.*

Table 3.16	<i>Cumulative Summary of Valid Licences and Permits under Contract no.</i>
	HY/2011/08

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-11/364/2009/E	22 Dec 2016	N/A	Valid
Notification of Works Under APCO	LCAC-EN-LE-00017	7 Mar 2014	N/A	Valid
	5213-121-L2837-01	19 Apr 2016	N/A	Valid
Registration as a Chemical	5213-151-L2837-02	24 May 2016	N/A	Valid
Waste Producer	5213-134-L2898-01	16 Nov 2015	N/A	Valid
	5213-134-L2952-01	12 May 2017	N/A	Valid
Billing Account under Waste Disposal Ordinance	7019640	27 Mar 2014	N/A	Valid
	GW-RS0419-18	24 May 2018	27 May 2018 to 28 Nov 2018	Valid
	GW-RS0779-18	29 Aug 2018	1 Sep 2018 to 28 Feb 2019	Valid
	GW-RS0257-18	27 Mar 2018	1 May 2018 to 30 Oct 2018	Valid
Construction Noise Permit (CNP) for non-piling equipment	GW-RS0323-18	23 Apr 2018	01 May 2018 to 30 Oct 2018	Valid
	GW-RS0335-18	26 Apr 2018	1 May 2018 to 31 Oct 2018	Valid
	GW-RS0357-18	02 May 2018	04 May 2018 to 02 Oct 2018	Valid
	GW-RS0434-18	30 May 2018	1 Jun 2018 to 30 Nov 2018	Valid



Permits and/or Licences	Reference No.	Reference No. Issued Date		Status
	GW-RS0435-18	30 May 2018	1 Jun 2018 to 30 Nov 2018	Valid
	GW-RS0440-18	30 May 2018	9 Jun 2018 to 28 Oct 2018	Valid
	GW-RS0445-18	30 May 2018	1 Jun 2018 to 30 Nov 2018	Valid
	GW-RS0452-18	31 May 2018	1 Jun 2018 to 30 Nov 2018	Valid
	GW-RS0548-18	26 Jun 2018	1 Jul 2018 to 31 Dec 2018	Valid
	GW-RS0547-18	26 Jun 2018	1 Jul 2018 to 31 Dec 2018	Valid
	GW-RS0613-18	13 Jul 2018	16 Jul 2018 to 12 Jan 2019	Valid
	GW-RS0630-18	18 Jul 2018	21 Jul 2018 to 30 Oct 2018	Valid
	GW-RS0659-18	27 Jul 2018	1 Aug 2018 to 31 Jan 2019	Valid
	GW-RS-0662-18	30 Jul 2018	1 Aug 2018 to 31 Jan 2019	Valid
	GW-RS0742-18	17 Aug 2018	20 Aug 2018 to 31 Oct 2018	Valid
	GW-RS0746-18	20 Aug 2018	24 Aug 2018 to 31 Jan 2019	Valid
	GW-RS0759-18	24 Aug 2018	27 Aug 2018 to 26 Feb 2019	Valid
	GW-RS0794-18	04 Sep 2018	15 Sep 2018 to 30 Nov 2018	Valid
	GW-RS0840-18	11 Sep 2018	13 Sep 2018 to 30 Nov 2018	Valid
	GW-RS0849-18	14 Sep 2018	17 Sep 2018 to 30 Nov 2018	Valid
	GW-RS0854-18	14 Sep 2018	17 Sep 2018 to 30 Nov 2018	Valid
	GW-RS0832-18	10 Sep 2018	12 Sep 2018 to 30 Nov 2018	Valid
	GW-RS0874-18	07 Sep 2018	10 Sep 2018 to 31 Oct 2018	Valid
	GW-RS0860-18	19 Sep 2018	21 Sep 2018 to 30 Nov 2018	Valid
	GW-RS0808-18	07 Sep 2018	10 Sep 2018 to 7 Feb 2019	Valid
	WT00022046-2015	1 Mar 2017	31 Jul 2019	Valid
Water Discharge License	WT00022753-2015	22 Jun 2017	30 Apr 2021	Valid



Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	WT00024561-2016	30 May 2016	31 May 2021	Valid
	WT00025858-2016	17 Oct 2016	31 Oct 2021	Valid
	WT00026829-2017	14 Jun 2017	31 Jan 2022	Valid
	WT00027343-2017	01 Mar 2017	31 Mar 2022	Valid
	WT000283434-2017	09 Aug 2017	31 Aug 2022	Valid

Table 3.17 Summary of submission status under FEP-11/364/2009/E

EP Condition	Submission	Date of Submission
Condition 2.9	Condition 2.9 Noise Management Plan (Rev.4)	
Condition 2.14	Landscape Plan (Rev.2)	18 Feb 2015
Condition 2.13 a)	Operational Air Quality Management Plan for West Ventilation Building (Rev.0)	25 Nov 2014
Condition 2.13 b) Operational Air Quality Management Plan for Central Ventilation Building (Rev.0)		03 Mar 2017
Condition 2.13 c)	Operational Air Quality Management Plan for East Ventilation Building and East Vent Shaft (Rev.0)	18 Feb 2015
Condition 2.13 d) Operational Air Quality Management Plan for an Electrostatic Precipitator system for EVB Operation (Rev.0)		06 Apr 2017
Condition 2.13 e) Operational Air Quality Management Plan for ventilation system of Eastern Portal of the CWB Tunnel (Rev.0)		23 Oct 2016



4 MONITORING REQUIREMENTS

4.1 Noise Monitoring

NOISE MONITORING STATIONS

4.1.1. The noise monitoring stations for the Project are listed and shown in *Table 4.1* and *Figure* <u>4.1.</u> <u>Appendix 4.1</u> shows the established Action/Limit Levels for the monitoring works.

Station	Description
M1a***	Footbridge for Ex-Harbour Road Sports Centre
M2b	Noon-day Gun Area
M3a	Tung Lo Wan Fire Station
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School
M7e*	International Finance Centre (Eastern End of Podium)
M7w	International Finance Centre (Western End of Podium)
M8**	City Hall

Table 4.1 Noise Monitoring Stations

Remark *: Location ID has been updated from M7 to M8 for City Hall

Remark **: M7e has become a reference station starting from 7 Aug 2012

Remarks***: The location ID of monitoring station M1a was updated as "Footbridge for Ex-Harbour Road Sports Centre" in May 2017.

REAL TIME NOISE MONITORING STATIONS

4.1.2. The noise monitoring stations for the Project are listed and shown in *Table 4.2* and <u>Figure</u> <u>4.1</u>. <u>Appendix 4.1</u> shows the established Action/Limit Levels for the monitoring works.

Table 4.2 Real Time Noise Monitoring Stations

District	Station	Description
Tin Hau	RTN1	FEHD Hong Kong Transport Section Whitfield Depot
North Point	RTN2a	Hong Kong Electric Centre
North Point	RTN3	Po Leung Kuk Yu Lee Mo Fan Memorial School
Tin Hau	RTN4	Causeway Bay Community Centre



NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.3. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level (Leq). Leq (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods, Leq (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO) criteria. Supplementary information for data auditing, statistical results such as L₁₀ and L₉₀ shall also be obtained for reference.
- 4.1.4. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
 - One set of measurements between 0700 and 1900 hours on normal weekdays.
- 4.1.5. Real time noise shall be carried out at the designated monitoring stations. The following is an initial guide on the regular monitoring frequency for each station on a 24 hours basis when noise generating activities are underway:
 - One set of measurements between 0700 and 1900 hours on normal weekdays.
 - One set of measurements between 1900 and 2300 hours on normal weekdays and 0700 and 2300 hours on public holidays.
 - One set of measurements between 2300 and 0700 hours on next day on everyday.
- 4.1.6. If construction works are extended to include works during the hours of 1900 0700 as well as public holidays and Sundays, additional weekly impact monitoring shall be carried out during respective restricted hours periods. Applicable permits under NCO shall be obtained by the Contractor.

MONITORING EQUIPMENT

- 4.1.7. As referred to in the Technical Memorandum [™] issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.
- 4.1.8. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.
- 4.1.9. The sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency before deployment to the site and during each site visit. Measurements will be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.



4.2 Air Quality Monitoring AIR QUALITY MONITORING STATIONS

4.2.1. The air quality monitoring stations for the Project are listed and shown in *Table 4.3 and Figure 4.1.* Appendix 4.1 shows the established Action/Limit Levels for the monitoring works.

Table 4.5 An Quanty Monitoring Stations		
Station ID	Monitoring Location	Description
CMA1b	Harbour Grand Hotel Boundary Wall**	North Point (Re- commenced on 14 November 2011)
CMA2a	Causeway Bay Community Centre	Causeway Bay
CMA3a	CWB PRE Site Office *	Causeway Bay
CMA4a	Society for the Prevention of Cruelty to Animals	Wan Chai
CMA5b	Pedestrian Plaza***	Wan Chai
MA1e	International Finance Centre (Eastern End of Podium)	Central
MA1w	International Finance Centre (Western End of Podium)	Central

Table 4.3 Air Quality Monitoring Stations

Remarks*: As per the ENPC meeting in March 2011, the monitoring stations CMA3a – Future CWB site office at Wanchai Waterfront Promenade was renamed as remark.

Remarks**: The location ID of monitoring station CMA1b was updated as "Oil Street Site Office" in April 2013. The location ID of monitoring station CMA1b was updated as "Harbour Grand Hotel Boundary Wall" with respect to the fine adjustment of monitoring station from the Oil Street Site Office to Harbour Grand Hotel Boundary Wall from 05 June 2017 onwards due to demolition of Oil Street Site Office.

Remarks***: The station ID and monitoring location was updated in December 2014 with respect to monitoring station relocation.

AIR QUALITY MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 4.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 4.2.4. For regular impact monitoring, the sampling frequency of at least once in every six days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six days should be undertaken when the highest dust impact occurs.



SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 4.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
 - 0.6 1.7 m³ per minute adjustable flow range;
 - Equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
 - Installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
 - Capable of providing a minimum exposed area of 406 cm2;
 - Flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
 - Equipped with a shelter to protect the filter and sampler;
 - Incorporated with an electronic mass flow rate controller or other equivalent devices;
 - Equipped with a flow recorder for continuous monitoring;
 - Provided with a peaked roof inlet;
 - Incorporated with a manometer;
 - Able to hold and seal the filter paper to the sampler housing at horizontal position;
 - Easily changeable filter; and
 - Capable of operating continuously for a 24-hour period.
- 4.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

LABORATORY MEASUREMENT / ANALYSIS

- 4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.
- 4.2.8. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24 hours and be pre-weighed before use for the sampling.
- 4.2.9. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.
- 4.2.10. All the collected samples shall be kept in a good condition for 6 months before disposal.
- 4.2.11. Current calibration certificates of equipments are presented in Appendix 4.2.



5 MONITORING RESULTS

- 5.0.1. The environmental monitoring will be implemented based on the division of works areas of each designated project managed under different contracts with separate FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in *Figure 2.1* and *Figure 4.1*. The monitoring results are presented in according to the Individual Contract(s).
- 5.0.2. In the reporting period, the concurrent contracts are as follows:
 - Contract no. HY/2009/19 Central Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link
 - Contract no. HY/2010/08 Central- Wanchai Bypass Tunnel (Slip Road 8 Section)
 - Contract no. HK/2009/02 Wan Chai Development Phase II Central Wan Chai Bypass at Wan Chai East
 - Contract no. HK/2012/08 Wan Chai Development Phase II Central Wan Chai Bypass at Wan Chai West
 - Contract no. HY/2011/08 Central Wan Chai Bypass (CWB)– Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning
- 5.0.3. The environment monitoring schedules for reporting period and coming month are presented in *Appendix 5.1*.



5.1 Noise Monitoring Results

5.1.1 Monitoring for report of review baseline noise level was performed from 11 April 2011 to 8 June 2011. Then the report was submitted on the 20 June 2011, verified by IEC on 18 July 2011 and was approved by ER by January 2012. The new baseline is used for the noise calculation starting from January 2012.

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East (CWB Tunnel) under FEP-01/364/2009</u>

5.1.2 The commencement of construction works for HK/2009/02 under FEP-01/364/2009 is on 26 April 2011. The proposed division of noise monitoring stations are summarized in *Table 5.2* below.

 Table 5.2
 Noise Monitoring Station for Contract no HK/2009/02

Station	Description
M1a	Footbridge for Ex-Harbour Road Sports Centre

- 5.1.3 No action or limit level exceedance was recorded in the reporting period.
- 5.1.4 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in <u>Appendix</u> <u>5.2.</u>

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

5.1.5 Noise monitoring for the tunnel works under contract no. HY/2009/19 was commenced on 24 April 2011. The proposed division of noise monitoring stations are summarized in *Table 5.4* below.

 Table 5.4
 Noise Monitoring Stations for Contract no. HY/2009/19

Station	Description
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School

- 5.1.6 No action or limit level exceedance was recorded in the reporting period.
- 5.1.7 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in <u>Appendix</u> <u>5.2</u>. Details of the Notification of Exceedance can be referred in <u>Appendix 6.2</u>.



<u>Contract no. HY/2010/08 – Central-Wanchai Bypass –Wanchai Bypass Tunnel (Slip Raod 8</u> <u>Section) under FEP-12/364/2009/D</u>

5.1.8 The commencement of construction works for Contract no. HY/2010/08 under FEP-10/364/2009/B was on 02 September 2013. Noise monitoring was commenced on 02 September 2013. The proposed divisions of noise monitoring stations are summarized in *Table 5.5* below.

Station	Description
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station
*M7e	International Finance Centre (Eastern End of Podium)
M7w	International Finance Centre (Western End of Podium)
M8	City Hall

 Table 5.5
 Noise Monitoring Stations for Contract no. HY/2010/08

* Remark: M7e has become a reference station starting from 7 Aug 2012

- 5.1.9 As confirmed with CWB RSS, junction modification works in Central area would be conducted by Contract HY/2010/08 starting from July 2018 and tentatively completed in September 2018. The noise monitoring station M7e - International Finance Centre (Eastern End of Podium), M7w - International Finance Centre (Western End of Podium) and M8 – City Hall would tentatively associated with Contract HY/2010/08.
- 5.1.10 No action or limit level exceedance was recorded in the reporting period.
- 5.1.11 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in <u>Appendix</u> <u>5.2.</u>

<u>Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems</u> and Fittings, and Works Associated with Tunnel Commissioning

5.1.12 Noise monitoring for the Central Interchange works under contract no. HY/2011/08 was commenced on 22 April 2011.The proposed division of noise monitoring stations for Contract no. HY/2011/08 are summarized in *Table 5.6* below:

Station	Description
M4b	Victoria Centre
*M7e	International Finance Centre (Eastern End of Podium)
M7w	International Finance Centre (Western End of Podium)
M8	City Hall

 Table 5.6
 Noise Monitoring Stations for Contract no. HY/2011/08

* Remark: M7e has become a reference station starting from 7 Aug 2012



- 5.1.13 No action or limit level exceedance was recorded in the reporting period.
- 5.1.14 Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in <u>Appendix</u> <u>5.2</u>.



5.2 Real Time Noise Monitoring Results

- 5.2.1. Real time noise monitoring at RTN4-Causeway Bay Community Centre was commenced on 13 Jan 2013. The baseline noise level of RTN4- Causeway Bay Community Centre has adopted the results from the baseline noise monitoring report for EP/364/2009 in 22 April 2010 in which approved by EPD.
- 5.2.2. Po Leung Kuk Yu Lee Mo Fan Memorial School granted permission for set up on 4 Sep 2012 and real time noise monitoring station RTN3 set up was performed on 14 Sep 2012. Real time noise baseline capturing was conducted during time period without construction work from 21 Sep 2012 to 04 Oct 2012. Real time noise monitoring at RTN3 Po Leung Kuk Yu Lee Mo Fan Memorial School was commenced since 06 Oct 2012.
- 5.2.3. Real-time noise monitoring station RTN2 previously located at oil Street Community Liaison Centre was relocated to Hong Kong Electric Centre on 5 Oct 2012, which is a representative of the noise sensitive receiver City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted at Hong Kong Electric Centre from 4 December 2009 to 17 December 2009.
- 5.2.4. Real-time noise monitoring station RTN1-FEHD Whitfield Depot was finely adjusted from 2/F to roof-top at FEHD Whitfield Depot on 24 June 2013 with respect to the commencement of advance works for IEC parapet demolition.
- 5.2.5. With respect to the non-CWB Project building construction at Oil Street, the real-time noise monitoring station RTN2a- Hong Kong Electric Centre was finely adjusted from Northeast Side to Northwestern side at Roof Top location on 03 March 2017.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

5.2.6. The proposed division of noise monitoring stations are summarized in *Table 5.7* below. Real time noise monitoring for major construction works under contract no. HY/2009/19 was commenced on 24 April 2011.

Location ID	District	Description
RTN1	Tin Hau	FEHD Hong Kong Transport Section Whitfield Depot
RTN2a	North Point	Hong Kong Electric Centre
RTN3	North Point	Po Leung Kuk Yu Lee Mo Fan Memorial School
RTN4	Tin Hau	Causeway Bay Community Centre

Table 5.7 Real Time Noise Monitoring Stations for Contract no. HY/2009/19

* Real time noise monitoring results and graphical presentation during restrict hours and night time period are for information only and noise during CNP period shall be controlled under NCO.



5.2.7. No limit level exceedance was recorded at RTN1 - FEHD Hong Kong Transport Section Whitfield Depot in the reporting period.

Lam Geotechnics Limited

- 5.2.8. No limit level exceedance was recorded at RTN2a Hong Kong Electric Centre in the reporting period.
- 5.2.9. Limit level exceedance was recorded on 13 September 2018 at RTN3 Yu Lee Mo Fan Memorial School in the reporting period. After checking with the Contractor, no construction activities was conducted under Contract HY/2009/19 around the monitoring station. In view of the above, the exceedance was considered as non-project related and potentially contributed by nearby IEC traffic.
- 5.2.10. No limit level exceedance was recorded at RTN4 Causeway Bay Community Centre in the reporting period.
- 5.2.11. Real time noise monitoring results measured in this reporting period are reviewed and summarized. Details of real time noise monitoring results and graphical presentation can be referred to *Appendix 5.4.*



<u>Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) – Tunnel Buildings,</u> <u>Systems and Fittings, and Works Associated with Tunnel Commissioning</u>

5.2.12. The proposed division of noise monitoring stations are summarized in *Table 5.8* below. Real time noise monitoring for major construction works under contract no. HY/2011/08 was commenced on 19 March 2015.

	<u> </u>		
Location ID	District	Description	
RTN1	Tin Hau	FEHD Hong Kong Transport Section Whitfield Depot	
RTN2a	North Point	Hong Kong Electric Centre	
RTN4	Tin Hau	Causeway Bay Community Centre	

 Table 5.8 Real Time Noise Monitoring Stations for Contract no. HY/2011/08

*Real time noise monitoring results and graphical presentation during restrict hours and night time period are for information only and noise during CNP period shall be controlled under NCO.

- 5.2.13. No limit level exceedance was recorded at RTN1 FEHD Hong Kong Transport Section Whitfield Depot in the reporting period.
- 5.2.14. No limit level exceedance was recorded at RTN2a Hong Kong Electric Centre in the reporting period.
- 5.2.15. No limit level exceedance was recorded at RTN4 Causeway Bay Community Centre in the reporting period.



5.3 Air Quality Monitoring Results

Lam Geotechnics Limited

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> Wan Chai East (CWB Tunnel) under FEP-01/364/2009

5.3.1 The commencement of construction works for HK/2009/02 under FEP-01/364/2009 is on 26 April 2011. The proposed division of air quality monitoring stations are summarized in *Table 5.11* below.

Table 5.11 Air Quality Monitoring Station for Contract no. HK/2009/02

Station	Description
CMA3a	CWB site office at Wanchai Waterfront Promenade
CMA4a	Society for the Prevention of Cruelty to Animals

- 5.3.2 No action or limit level exceedance was recorded in the reporting period.
- 5.3.3 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in <u>Appendix 5.3</u>.

<u>Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and</u> <u>Island Eastern Corridor Link under FEP-07/364/2009/D</u>

5.3.4 The proposed division of air quality monitoring stations are summarized in *Table 5.13* below. Air quality monitoring for the tunnel works under contract no. HY/2009/19 was commenced on 26 April 2011.

Table 5.13 Air Quality Monitoring Stations for Contract no. HY/2009/19

Station	Description
CMA1b	Harbour Grand Hotel Boundary Wall
CMA2a	Causeway Bay Community Centre

- 5.3.5 No action or limit level exceedance was recorded in the reporting period,
- 5.3.6 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in <u>Appendix 5.3</u>.



Contract no. HK/2012/08- Wan Chai Development Phase II – Central-Wan Chai Bypass at Wan Chai West

5.3.7 The commencement of construction works for Contract no. HK/2012/08 under FEP-09/364/2009/B was on May 2014. Air quality monitoring was commenced on 25 August 2011. The proposed division of air quality monitoring stations are summarized in **Table 5.14** below.

Table 5.14 Air Quality Monitoring Station for Contract no. HK/2012/08

Station	Description
CMA5b	Pedestrian Plaza

5.3.8 No action or limit level exceedance was recorded in the reporting period.

Lam Geotechnics Limited

5.3.9 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in *Appendix 5.3*.

<u>Contract no. HY/2010/08 – Central-Wanchai Bypass –Wanchai Bypass Tunnel (Slip Raod 8</u> <u>Section) under FEP-12/364/2009/D</u>

5.3.10 The commencement of construction works for Contract no. HY/2010/08 under FEP-12/364/2009/D was on July 2014. Air quality monitoring was commenced on 14 July 2011. The proposed division of air quality monitoring stations are summarized in *Table 5.15* below.

Table 5.15 Air Quality Monitoring Station for Contract no. HY/2010/08

Station	Description
CMA3a	CWB PRE Site Office
MA1e	International Finance Centre (Eastern End of Podium)
MA1w	International Finance Centre (Western End of Podium)

- 5.3.11 As confirmed with CWB RSS, junction modification works in Central area would be conducted by Contract HY/2010/08 starting from July 2018 and tentatively completed in September 2018. The noise monitoring station MA1e - International Finance Centre (Eastern End of Podium) and MA1w - International Finance Centre (Western End of Podium) would tentatively associated with Contract HY/2010/08.
- 5.3.12 No action or limit level exceedance was recorded in the reporting period.
- 5.3.13 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in <u>Appendix 5.3</u>.



<u>Contract no. HY/2011/08 – Central - Wan Chai Bypass (CWB) – Tunnel Buildings, Systems</u> and Fittings, and Works Associated with Tunnel Commissioning

5.3.14 Air quality monitoring for the Central Interchange works under contract no. HY/2011/08 was commenced on 21 April 2011. The proposed division of air quality monitoring stations are summarized in *Table 5.16* below.

Station	Description
MA1e	International Finance Centre (Eastern End of Podium)
MA1w	International Finance Centre (Western End of Podium)
CMA1b	Harbour Grand Hotel Boundary Wall
CMA2a	Causeway Bay Community Centre
CMA5b	Pedestrian Plaza

 Table 5.16 Air Quality Monitoring Stations for Contract no. HY/2011/08

- 5.3.15 No action or limit level exceedance was recorded in the reporting period.
- 5.3.16 Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air quality monitoring results and graphical presentation can be referred in *Appendix 5.3*.



5.4 Waste Monitoring Results

Lam Geotechnics Limited

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> Wan Chai East (CWB Tunnel) under FEP-01/364/2009

5.4.1. Inert C&D & non-inert C&D wastes were disposed of in this reporting period. Details of the waste flow table are summarized in *Table 5.18*.

Waste Type	Quantity this month	Cumulative Quantity- to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	0.0	531933.14	TKO137, TM 38
Inert C&D materials recycled, m ³	Nil	46520	N/A
Non-inert C&D materials disposed, m ³	29.0	5919.67	SENT Landfill
Non-inert C&D materials recycled, m ³	Nil	N/A	N/A
Chemical waste disposed , kg	Nil	17718	N/A
Marine Sediment (Type 1 – Open Sea Disposal) , m ³	Nil	65663	South Cheung Chau

 Table 5.18 Details of Waste Disposal for Contract no. HK/2009/02

Contract no. HY/2009/18 – Central – Wan Chai Bypass (CWB) – Central Interchange under FEP-05/364/2009/A

5.4.2. Inert C&D and non-inert C&D waste was disposed of in this reporting period. Details of the waste flow table are summarized in *Table 5.19*.

 Table 5.19 Details of Waste Disposal for Contract no. HY/2009/18

Waste Type	Quantity this month	Cumulative-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	Nil	1415580.18	T.K.O. 137, TM 38
Inert C&D materials recycled, m ³	Nil	58787.05	N/A
Non-inert C&D materials disposed, m ³	Nil	4572.26	SENT Landfill
Non-inert C&D materials recycled , ton	Nil	878.37	N/A
Chemical waste disposed, kg	Nil	6772	N/A



<u>Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon</u> <u>Shelter Section) under FEP-06/364/2009/A</u>

5.4.3. Inert & Non-inert C&D wastes were disposed of in this reporting period. Details of the waste flow table are summarized in *Table 5.20*.

Waste Type	Quantity this month	Cumulative Quantity-to- Date	Disposal / Dumping Grounds
Inert C&D materials	Nil	625200.92	Tuen Mun Area 38
disposed, m ³	Nil	245453.3	TKO137 FB
			HY/2009/11
			ex-PCWA
			TS4 /TS2
Inert C&D materials recycled, m ³	Nil	358660.77	WDII
			Lun Ku Tan
			WENT
			HY/2010/08
Non-inert C&D	Nil	4675.67	SENT Landfill
materials disposed, m ³	Nil	1.58	WENT Landfill
Non-inert C&D materials recycled, m ³	Nil	5496446.2	Xun Xiang Metalware Skylight Recycle (paper)
Chemical waste disposed , kg	Nil	22755	Dunwell Group
Marine Sediment (Type1-Open Sea Disposal (Dedicate Sites) &Type 2 – Confined Marine Disposal), m ³	Nil	5684	South of the Brothers

Table 5 20	Details of Waste Disposal for Contract no. HV/2000	/15
Table 5.20	Details of Waste Disposal for Contract no. HY/2009	//15



<u>Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D</u>

5.4.4. Inert and Non-inert C&D wastes were disposed of in this reporting period. Details of the waste flow table are summarized in *Table 5.21*.

Waste Type	Quantity this month	Cumulative-to- Date	Disposal / Dumping Grounds
Inert C&D materials disposed, ton	4584.10	807284.20	TM38
Inert C&D materials recycled, ton	Nil	82349.7	N/A
Non-inert C&D materials disposed, ton	232.30	8225.51	SENT Landfill
Non-inert C&D materials recycled, ton	Nil	565.63	N/A
Chemical waste disposed, ton	Nil	15.58	N/A
Marine Sediment (Tunnel) (Type-1 Open Sea Disposal), m ³	Nil	20737.96	South of Cheung Chau
Marine Sediment (Tunnel) (Type 1- Open Sea Disposal (Dedicated Sites) & Type 2 – Confined Marine Disposal), m ³	Nil	30751	East of Sha Chau
Marine Sediment (Approach Ramp) (Type 2 – Confined Marine Disposal), m3	Nil	6491	East of Sha Chau

Table 5.21 Details of Waste Disposal for Contract no. HY/2009/19



Contract no. HK/2012/08 Wan Chai Development Phase II - Central-Wan Chai Bypass at Wan Chai West under FEP-12/364/2009/D

5.4.5. No inert and Non-inert C&D wastes were disposed of in this reporting period. Details of the waste flow table are summarized in *Table 5.22*.

Waste Type	Quantity this month*	Cumulative-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m ³	56 35	184989 117669	ТКО 137 ТМ38
Inert C&D materials recycled, m³	Nil	Nil	N/A
Non-inert C&D materials disposed, m ³	105	9582	SENT
Non-inert C&D materials recycled, m ³	Nil	Nil	N/A
Chemical waste disposed , kg	Nil	Nil	N/A
Marine sediment (Type 1) disposal , m ³	Nil	3145	South of Cheung Chau / East of Sha Chau / South of The Brothers

Table 5.22 Details of Waste Disposal for Contract no. HK/2012/08

<u>Contract no. HY/2010/08 Central – Wan Chai Bypass (CWB) – Tunnel (Slip Road 8) under</u> <u>FEP-10/364/2009/B</u>

5.4.6. No inert and Non-inert C&D wastes were disposed of in this reporting period. Details of the waste flow table are summarized in *Table 5.23*.

Waste Type*	Quantity this month	Cumulative-to-Date	Disposal / Dumping Grounds
	584.91	596597.74	TM 38 / CW / TKO137SF
Inert C&D materials	Nil	262656.6	WENT
disposed, m ³	Nil	82911.8	SENT
	Nil	72704.53	TKO area 137
Inert C&D materials recycled, m ³	Nil	Nil	N/A
Non-inert C&D materials disposed , m ³	83.889	6231.74	SENT / WENT
Non-inert C&D materials recycled, m ³	Nil	Nil	N/A
Chemical waste disposed , kg	Nil	1431	N/A
Type 1 – Open Sea Disposal, m ³	Nil	16368.4	East Sha Chau/ South Brothers Island
Type 2 – Confined Marine disposal, m ³	Nil	549.2	East Sha Chau



<u>Contract no. HY/2011/08 Central – Central - Wan Chai Bypass (CWB) – Tunnel Buildings,</u> Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E

5.4.7. No inert and Non-inert C&D wastes were disposed of in this reporting period. Details of the waste flow table are summarized in *Table 5.24*.

Waste Type*	Quantity this month	Cumulative-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed , m ³	464.694	6842.907	CWPF & TKO137
Inert C&D materials recycled, m ³	Nil	Nil	N/A
Non-inert C&D materials disposed , m ³	267.444	8070.272	SENT
Non-inert C&D materials recycled , ton	18.08	257.67	N/A
Chemical waste disposed, kg	Nil	3800	N/A

Table 5.24 Details of Waste Disposal for Contract no. HY/2011/08



6 COMPLIANCE AUDIT

6.0.1. The Event Action Plan for construction noise, air qualities are presented in <u>Appendix 6.1</u>.

6.1 Noise Monitoring

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East (CWB Tunnel) under FEP-01/364/2009</u>

6.2.1. No action or limit level exceedance was recorded in the reporting period.

<u>Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and</u> <u>Island Eastern Corridor Link under FEP-07/364/2009/D</u>

6.2.2. No action or limit level exceedance was recorded in the reporting period.

Contract no. HY/2010/08 – Central-Wanchai Bypass – Tunnel (Slip Raod 8 Section) under FEP-10/364/2009/B

6.2.3. No action or limit level exceedance was recorded in the reporting period.

Contract no. HY/2011/08 Central –Central - Wan Chai Bypass (CWB) –Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E

6.2.4. No action or limit level exceedance was recorded in the reporting period.

6.2 Real Time Noise Monitoring

<u>Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and</u> <u>Island Eastern Corridor Link under FEP-07/364/2009/D</u>

- 6.2.1. No limit level exceedance was recorded at RTN1 FEHD Hong Kong Transport Section Whitfield Depot in the reporting period.
- 6.2.2. No limit level exceedances was recorded at RTN2a Hong Kong Electric Centre in the reporting period.
- 6.2.3. Limit level exceedances was recorded on 13 September 2018 at RTN3 Yu Lee Mo Fan Memorial School in the reporting period. After the investigation, the exceedance was concluded as non-Project related.
- 6.2.4. No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre in the reporting period.



<u>Contract no. HY/2011/08 Central – Central - Wan Chai Bypass (CWB) – Tunnel Buildings,</u> <u>Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E</u>

- 6.2.5. No limit level exceedance was recorded at RTN1 FEHD Hong Kong Transport Section Whitfield Depot in the reporting period.
- 6.2.6. No limit level exceedance was recorded at RTN2a Hong Kong Electric Centre in the reporting period.
- 6.2.7. No limit level exceedance was recorded at RTN4- Causeway Bay Community Centre in the reporting period.
- 6.3 Air Quality Monitoring

<u>Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at</u> <u>Wan Chai East (CWB Tunnel) under FEP-01/364/2009</u>

6.3.1. No action or limit level exceedance was recorded in the reporting period.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link under FEP-07/364/2009/D

6.3.2. No action or limit level exceedance was recorded in the reporting period.

Contract no. HK/2012/08 Wan Chai Development Phase II - Central-Wan Chai Bypass at Wan Chai West under FEP-12/364/2009/D

6.3.3. No action or limit level exceedance was recorded in the reporting period.

<u>Contract no. HY/2010/08 – Central-Wanchai Bypass – Tunnel (Slip Raod 8 Section) under FEP-10/364/2009/B</u>

6.3.4. No action or limit level exceedance was recorded in the reporting period.

<u>Contract no. HY/2011/08 Central – Central - Wan Chai Bypass (CWB) – Tunnel Buildings,</u> <u>Systems and Fittings, and Works Associated with Tunnel Commissioning under FEP-11/364/2009/E</u>

6.3.5. No action or limit level exceedance was recorded in the reporting period.

6.4 Review of the Reasons for and the Implications of Non-compliance

6.4.1 There was no non-compliance from the site audits in the reporting period. The observations and recommendations made in each individual site audit session were presented in Section 8.

6.5 Summary of action taken in the event of and follow-up on non-compliance

6.5.1 No particular action taken was taken for site audits since no non-compliance was recorded in the reporting period.



7 CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS

- 7.0.1. According to Condition 3.4 of the EP-364/2009/E, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) and Wan Chai Development Phase II Central Wan Chai Bypass at Wan Chai East (CWB Tunnel).
- 7.0.2. According to the Final EM&A Report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011. As such, it is considered that there were no cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) undertaken by contractor HK12/02 in the reporting period.
- 7.0.3. According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area include roadworks, drainage and seawall coping were performed in September 2018 reporting period. As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were road and drains construction and removal of temporary reclamation at Wan Chai. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were ventilation building construction junction modification at Central; reinstatement works along Causeway Bay Typhoon Shelter, road works and landscape works at Victoria Park; bridge construction, approach ramp construction, landscape deck construction, drainage construction and ventilation building construction at North Point area in the reporting period. In addition, other non-Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects were observed undertaken at Wan Chai North and North Point area.
- 7.0.5. As relevant site mitigation measures for air quality and construction noise were implemented, no significant air quality impact and noise impact from construction activities was concluded in the reporting period. Besides, no project related exceedance was recorded during the air quality and noise environmental monitoring events in the reporting period. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) was insignificant.



8 ENVIROMENTAL SITE AUDIT

- 8.0.1. During this reporting period, weekly environmental site audits were conducted for Contracts HY/2009/19, HK/2012/08, HK/2009/02, HY/2010/08 and HY/2011/08. No non-conformance was identified during the site audits. The Contractors rectified major observations and recommendations made during the audit sessions.
- 8.0.2. Site inspections for Contract no. HY/2009/19 were carried out during this reporting period.
 No observation was found in the reporting period. The results of these inspections and outcomes are summarized in *Table 8.4*

ltem	Date	Observations	Action taken by Contractor	Completion date
180829_1	29 August 2018	Contractor shall tighten or extend the silt curtains to avoid muddy dispersion (Area near EVB)	Silt curtains was tighten and no further muddy dispersion was observed	Completion as observed on 5 September 2018

Table 8.4 Summary of Environmental Inspections for Contract no. HY/2009/19

8.0.3. Site inspections for Contract no. HK/2009/02 were carried out during this reporting period. The results of these inspections and outcomes are summarized in *Table 8.5.*

ltem	Date	Observations	Action taken by Contractor	Completion date
180830_1	30 August 2018	Silt curtain shall be extend and enclose the marine works area. The damaged silt section of silt curtain shall be repair to avoid muddy dispersion. (Portion 3&4)	Marine works was suspended	Completed as observed on 6 September 2018
180906_1	6 September 2018	Contractor shall seal the hole at gate B.	The hole at gate B was sealed.	Completed as observed on 12 September 2018

Table 8.5 Summary of Environmental Inspections for Contract no. HK/2009/02

8.0.4. Site inspection for Contract no. HK/2012/08 were carried out during this reporting period. The results of these inspections and outcomes are summarized in *Table 8.6*

Table 8.6	Summary of Environmental Inspections for Contract no. HK/2012/08

ltem	Date	Observations	Action taken by Contractor	Outcome	
180926_1	26 September 2018	Contractor shall keep the public road clean.	The site access was cleaned properly.	Completion as observed on 2 October 2018	



- 8.0.5. Site inspections for Contract no. HY/2010/08 were carried out during this reporting period. No observation was found in the reporting period.
- 8.0.6. Site inspections for Contract no. HY/2011/08 were carried out during this reporting period. No observation was found in the reporting period.



9 COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION

9.0.1. One environmental complaint was received in the reporting period.

An EPD complaint was referred to the ET on 3 September 2018 (CASE Ref: H08/RS/00024048-18). The complainant reported that: Night time construction noise on Island Eastern Corridor outside Provident Centre at around 1:00 a.m. on 31st August, 2018. ET confirmed with the Resident Site Staff that 1) There was no construction activity undertaken by Contract HY/2011/08 at Island Eastern Corridor during the restricted hours from 2300hrs on 30 August 2018 to 0700hrs on 31 August 2018. 2) The Contractor of HY/2009/19 reported that paving work was conducted during the period of 0100hrs to 0600hrs at 31 August 2018 at the works area from D12 to F8 where was located inside the noise semi-enclosure of IEC. Total 4 nos. dump truck, 1 nos. paver, 1 no. vibratory roller and 1no. road roller with QPME label were used for the paving work.

Relevant Construction Noise Permit GW-RS0679-18 was in place for the construction works conducted during the above concerned periods. The PMEs operated during the concerned period was included in Construction Noise Permit GW-RS0679-18 Condition 3.a. Group F. Based on RSS information, the noise control measure listed in Construction Noise Permit GW-RS0679-18 Condition 3.d.9 including installation of engine exhaust silencers for asphalt paver and installation of absorbing lining to the engine compartment for road roller and vibratory roller were generally in place. Meanwhile, there is no sufficient information to conclude if the concerned asphalt paver installed with absorbing lining to the engine compartment; and concerned road roller and vibratory roller installed with engine exhaust silencers according to Construction Noise Permit GW-RS0679-18 Condition 3.d.9.

In view of the above, the Contractor of HY/2009/19 was advised to critically check and confirm the noise control measures listed in Construction Noise Permit GW-RS0679-18 Condition 3.d.9 for concerned PMEs to ensure the operation of PMEs shall strictly follow the construction noise permit condition. The Contractor of HY/2009/19 was also reminded to maintain regular checking and maintenance of the PMEs and it's noise control measures deployed to avoid potential nuisance to the nearby public.

- 9.0.2. The details of cumulative complaint log and updated summary of complaints are presented in <u>Appendix 9.1</u>
- 9.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in *Table 9.1* and *Table 9.2* respectively.

Reporting Period	No. of Complaints
September 2018	1
September 2010 – August 2018	95
Total	96

 Table 9.1
 Cumulative Statistics on Complaints



Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date		
Air	1	0	1		
Noise	1	0	1		
Water	0	0	0		
Waste	0	0	0		
Total	2	0	2		

Lam Geotechnics Limited

Table 9.2 Cumulative Statistics on Successful Prosecutions



10 CONCLUSION


- 10.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.
- 10.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in *Table 10.1*. The construction programmes of individual contracts are provided in <u>Appendix 10.1</u>.

Contract No.	Key Construction Works	Recommended Mitigation Measures					
HY/2009/19	 Approach ramp structure, drainage and noise enclosure construction works Bridge noise enclosure installation works FEHD re-provision works Oil Street drainage works Watson Road Watermains laying works Hing Fat Street road and drainage works Trough B & C construction SR13 drainage works Seawall block reinstatement near box culvert T1 Landscape deck soft landscaping works 	 Noise level shall be controlled by reducing the breaking operation rate. Noise barrier shall be implemented Dust control during dust generating works Ensure proper deployment of silt curtain around marine construction works area Provide protection works and adequate drainage system to ensure no direct discharge into public drainage system or the sea. 					
HK/2012/08	 Construction of Slip Road 1 Construction of drainage Construction of roundabout 	 Dust control during dust generating works Provide protection works and adequate drainage system to ensure no direct discharge into public drainage system. 					

Table 10.1 Summary of Key Construction Activities of Individual Contract(s) to be commenced in Coming Reporting period



HY/2010/08	 Tree replanting works in VP, Drainage improvement works, Utility diversion works, Retaining wall works Junction modification 	 Dust control during dust generating works and stockpile stored on site. Appropriate measures should be taken to ensure adequate protections are provided for trees being transplanted and retained on site. Provision of protection to ensure no runoff out of site area or direct discharge into public drainage system.
HK/2009/02	 New PMMA for the replacement of 8 nos. of damaged PMMA panels Drainage work Backfilling behind seawall block Removal of temporary reclamation of TWCR4 Saw cutting of Northern D-Wall Pipe piling works for Box Culvert O Bay 12 and construction of DN1200 pipe Drainage connection works for Box Culvert O Bay 12 Demolition of existing Box Culvert O Bay 12 Construction of earthing platform for pipe piling works at Box Culvert O Bay 12 Fabrication of seawall blocks Backfilling and road works for Hung Hing Road at-grade Road Temporary drainage system for stock piling at Portion 5 DN600 sewerage works across Hung Hing Road Remedial works for covered walkway at Expo Drive East 	 Dust control during dust generating works Proper maintenance boundary surface runoff protection and water treatment facilities to avoid potential runoff related impact Ensure proper deployment of silt curtain around marine construction works area Provision of protection measures to ensure no runoff out of site area or direct discharge into public drainage system.





HY/2011/08	ABWF works at Ventilation	Dust control during dust generating
	Buildings, inclusive of Administration	works
	Building, Central Ventilation	
	Building, East Ventilation	
	Shaft/Building, West Ventilation	
	Building	
	Construction works at SCB and	
	SCP area	
	Application of road marking inside	
	the Tunnel, asphalt pavement	
	Installation and testing of Electricals	
	and Mechanicals	
	Installation of Tunnel Features	
	Man Po Street widening works	
	Traffic sign installation and	
	modification of directional sign at	
	various locations	

10.0.3. The construction works of Contract no. 04/HY/2006 – Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street under FEP-04/364/2009/A was completed, and the FEP was surrendered by the Contractor on 11 February 2011.

- 10.0.4. The construction works of Contract no. HY/2009/17 Advance piling works at Whitfield Depot under FEP-03/264/2009 was completed, and the FEP was surrendered by the Contractor and found in order by EPD on 25 April 2013.
- 10.0.5. The construction works of Contract HK/2010/06 was completed, and the FEP-08/364/2009/A was surrendered by the Contractor on 3 October 2014.
- 10.0.6. The Construction works under HY/2009/15 was confirm completed by the RSS from 27 October 2017 onwards.
- 10.0.7. The Construction works under HY/2009/18 was confirm completed by the RSS from 25 April 2018 onwards
- 10.0.8. As confirmed with WDII RSS and with respect to the joint inspection conducted with IEC on 25 May 2018, RSS, ET and IEC share the view that there is no adverse environmental impact of remaining works under Contract HK/2009/01 and the respective environmental site inspection was temporary suspended from 26 May 2018 onwards. FEP-02/364/2009 was surrendered by the Contractor on 3 September 2018.



Figure 2.1

Project Layout

COVERED BY APPROVED WD II & CWB EIA REPORT

1

COVERED BY APPROVED CWB & IECL EIA REPORT



Figure 2.2

Project Organization Chart




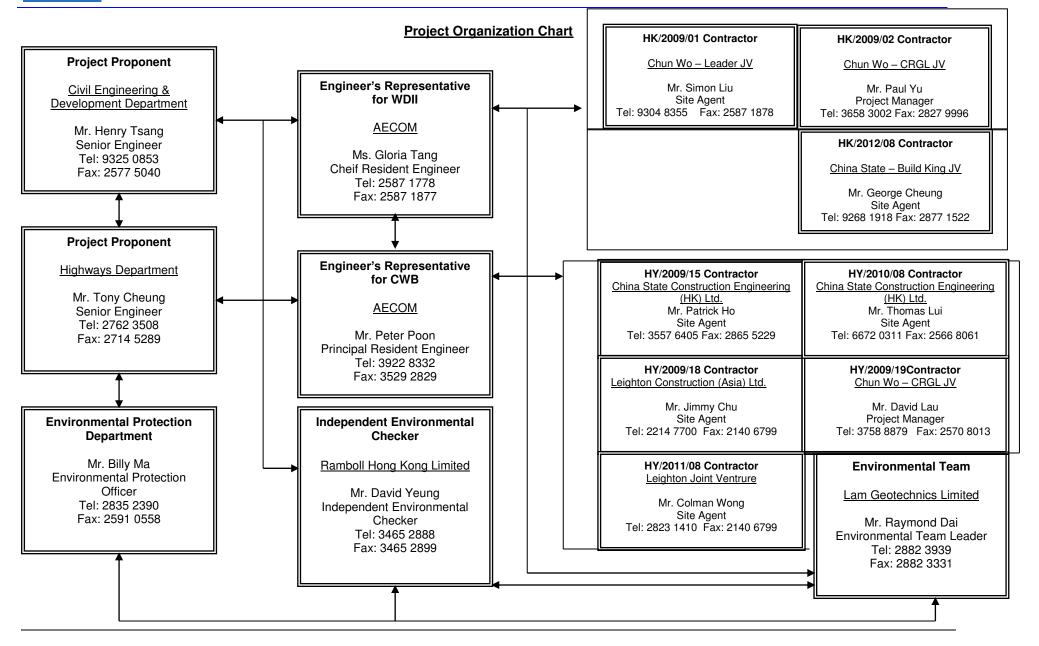




Figure 4.1

Locations of Monitoring Stations

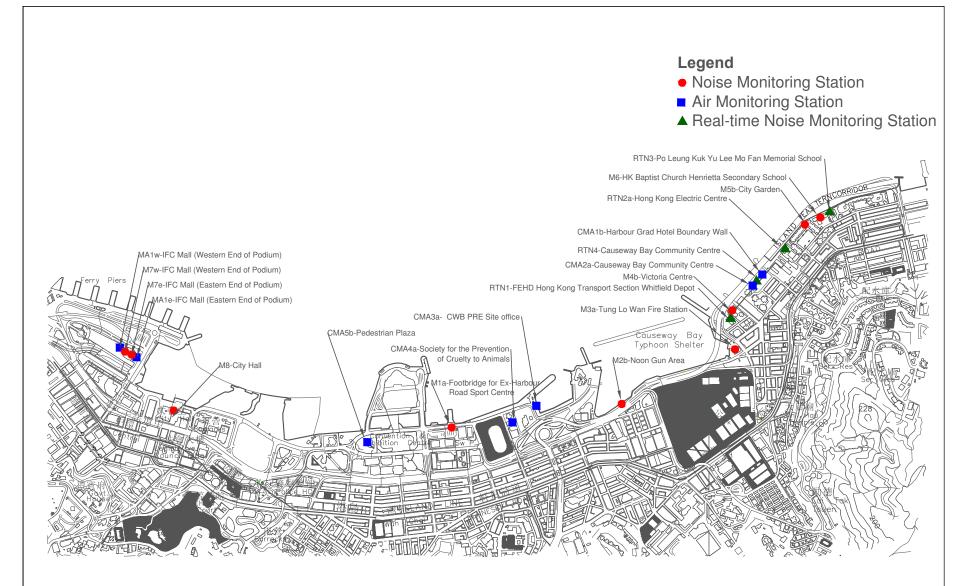

LOCATIONS OF AIR QUALITY AND NOISE MONITORING STATIONS



Appendix 3.1

Environmental Mitigation Implementation Schedule

Table A.1 Implementation Schedule for Air Quality Control

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation
Report Ref				Des	С	0	Dec	and Guidelines
Constructio								
S3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor					EIAO-TM
\$3.8.1	 Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts. Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition; Watering during excavation and material handling; Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations. 	Work site / during construction	Contractor		V			
Operational								
S3.6.53 – S3.6.54	The design parameters of the East and Central Ventilation Buildings as set in Tables 3.10 and 3.11 of Volume 1 of the WDII & CWB EIA Report.	East and Central Ventilation Buildings / During operation of the Trunk Road	HyD			V		
\$3.10.2	Air quality monitoring for the operation performance of the East Ventilation Building and associated East Vent Shaft will be conducted.	East Vent Shaft / During operation of the East Ventilation Building and associated East Vent Shaft	HyD			V		EIAO-TM

* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Monthly EM&A Report

Contract No. HK/2015/01 Wanchai Development Phase II and Central Wanchai Bypass Sampling, Field Measurement and Testing Work (Stage 3)

Table A.2Implementation Schedule for Noise Control

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation
Report Ref	Environmental i rotection weasures / whitgation weasures			Des	С	0	Dec	and Guidelines
Constructio	Construction Phase							
S4.9.3	 Good Site Practice: Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program. Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program. Mobile plant, if any, shall be sited as far away from NSRs as possible. Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum. Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. 	Work Sites / During Construction	Contractor		V			EIAO-TM, NCO
S4.8.1 – S4.8.11	 Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from onsite construction activities. Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks: Slip road 8 tunnel Construction of diaphragm wall and substructures of the tunnel approach ramp Excavation Construction of slabs Backfill 	Work Sites / During Construction	Contractor					EIAO-TM, NCO

Monthly EM&A Report

Contract No. HK/2015/01

Wanchai Development Phase II and Central Wanchai Bypass Sampling, Field Measurement and Testing Work (Stage 3)

Monthly EM&A Report

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	tion / Timing Implementation Agent Implementation Stages* Relevant Legislation and Guidelines						
Report Ref	Environmental i fotection measures / mitigation measures		Agent	Des	С	0	Dec	and Guidelines	
	 Demolition and construction of substructures for the IEC Demolition works of existing piers and crossheads of the marine section of the existing IEC Use of PME grouping for the following tasks: At-grade road construction Substructure for IECL connection 								
Operation I	Phase								
\$4.8.12 - \$4.8.23	 For Existing NSRs about 235m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC about 230m length of noise semi-enclosure with transparent panel covering the main carriageways (eastbound and westbound) of the CWB and IEC about 135m length of 5.5m high cantilevered noise barrier with 4.5m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC (amended under EP-364/2009/A) about 95m length of 5.5m high cantilevered noise barrier with 1m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC 	Near North Point / Before commencement of operation of road project	HyD	V	~	\checkmark		EIAO-TM	

Monthly EM&A Report

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	Im		ientat ges*	ion	Relevant Legislation
Report Ref	In momentaria roccoson neusaros / magavion neusaros	Location / Thining	Agent	Des	С	0	Dec	and Guidelines
	 For Future/Planned NSRs about 265m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC 	In between the Electric Centre (next to City Garden) and CDA(1) site / Before occupation of Planned NSRs in CDA and CDA(1) sites.	HyD	V	√ #			
	• The openable windows of the temple, if any, should be orientated so as to avoid direct line of sight to the existing Victoria Park Road as far as practicable.	Near Causeway Bay Fire Station / During detailed design of the re- provisioned Tin Hau Temple	Project Proponent for the re-provisioned Tin Hau Temple	\checkmark				

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Only the steel frame for this section of noise semi-enclosure would be erected in advance during the construction of the westbound slip road.

Contract No. HK/2015/01

Wanchai Development Phase II and Central Wanchai Bypass Sampling, Field Measurement and Testing Work (Stage 3)

Table A.4 Implementation Schedule for Waste Management

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Sta	entati ges*	on	Relevant Legislation
Report Ref	Environmental i rotection Measures / Mitigation Measures		Agent	Des	С	0	Dec	and Guidelines
Constructio	on Phase							
S6.5.14	<i>Floating Refuse</i> During the construction phase, the project proponent's contractor will be responsible for the collection of any refuse within their works area. Floating booms will be provided on the water surface to confine the refuse from the working barges as well as to avoid the accumulation of pollutants within temporary embayment as mentioned in Table D9.3.	Work site / During the construction period	Contractor		\checkmark			
S6.6.1	 Good Site Practices Recommendations for good site practices during the construction activities include: nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site; training of site personnel in proper waste management and chemical waste handling procedures; provision of sufficient waste disposal points and regular collection for disposal; appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers; regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and a recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites). 	Work site / During the construction period	Contractor		V			Waste Disposal Ordinance (Cap.354)

Monthly EM&A Report

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Stag		on	Relevant Legislation
Report Ref	Environmental Frotection Measures / Mitigation Measures	Location / Timing	Agent	Des	С	0	Dec	and Guidelines
S6.6.2	 <i>Waste Reduction Measures</i> Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include: segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; to encourage collection of aluminium cans, PET bottles and paper, separate labelled bins shall be provided to segregate these wastes from other general refuse generated by the work force; any unused chemicals or those with remaining functional capacity shall be recycled; use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&D material. prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill; proper storage and site practices to minimise the potential for damage or contamination of construction materials; and plan and stock construction materials carefully to minimise amount of waste. 	Work site / During planning and design stage, and construction stage	Contractor		\checkmark			

Monthly EM&A Report

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	nplem Stag	entati ges*	on	Relevant Legislation
Report Ref	Environmental Frotection Measures / Mitigation Measures	Location / Thinnig	Agent	Des	С	0	Dec	and Guidelines
\$6.6.4	General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material. A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.		Contractor		V			Public Health and Municipal Services Ordinance (Cap. 132)
\$6.6.5	<i>Chemical Wastes</i> After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	Contractor		V			Waste Disposal (Chemical Waste) (General) Regulation Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.6.6	<i>Construction and Demolition Material</i> C&D material shall be sorted on-site into inert C&D material (that is, public fill) and C&D waste. All the suitable inert C&D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.	Work site / During the construction period	Contractor		\checkmark			ETWB TCW No. 33/2002, 31/2004, 19/2005

Monthly EM&A Report

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	In	ıplem Staş	entati ges*	on	Relevant Legislation
Report Ref	Environmental i rotection measures / mugation measures	Location / Thining	Agent	Des	С	0	Dec	and Guidelines
\$6.6.7	In order to monitor the disposal of public fill and C&D waste at public fill reception facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.	Work site / During the construction period	Contractor and Independent Environmental Checker		\checkmark			ETWB TCW No. 31/2004
\$6.6.8	 Bentonite Slurry The disposal of residual used bentonite slurry shall follow the good practice guidelines stated in ProPECC PN 1/94 "Construction Site Drainage" and listed as follows: If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis. If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters. If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal. 	Work site / During the construction period	Contractor		\checkmark			ProPECC PN 1/94

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Table A.5	Implementation Schedule for Land Contamination
-----------	--

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation	Implementation Stages*			on	Relevant Legislation
Report Ref		Agent Des C O Dec and Guidelines						
Constructio	on and Operation Phase							
S.7.1.1	As no potential contaminative land uses were identified within the Study Area, adverse land contamination impacts associated with the construction and operation of the Project is not expected. As such, environmental protection and mitigation measures are considered not necessary and will not be covered in this EM&A Manual.	-	-					-

* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

Monthly EM&A Report

WDII & CWB EIA	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	In	-	entati ges*	on	Relevant Legislation and Guidelines
Report Ref				Des	С	0	Dec	
Construction P	hase		-	•				
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored fo re-use in the construction of the soft landscape works where practical.	-	Contractor	\checkmark	\checkmark			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor		\checkmark			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor		\checkmark			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	\checkmark	\checkmark			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		\checkmark			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor					EIAO TM
Operation Pha		- 1	1					
Table 10.6, Figure 10.5.1- 10.5.5	OM1 Aesthetic design of buildings and road-related structures including viaducts, vent buildings, subways, footbridge and noise barriers and enclosure.		HyD	V	\checkmark	\checkmark		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1- 10.5.5	OM3 Buffer Tree and Shrub Planting to screen proposed road and associated structures.	Work site / During Design Stage and Operation Phases	HyD	\checkmark	\checkmark	\checkmark		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1- 10.5.5	OM5 Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	HyD	\checkmark	\checkmark	\checkmark		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1- 10.5.5	OM6 Aesthetic design of roadside amenity areas.	Work site / During Design Stage and Operation Phases	HyD		V	V		ETWB TCW 2/2004

Table A.7 Implementation Schedule for Landscape and Visual

*Des - Design, C - Construction, O – Operation, and Dec - Decommissioning



Appendix 4.1

Action and Limit Level



Lam Geotechnics Limited

Action and Limit Level

Action and Limit Level for Noise Monitoring

Time Period	Action Level	Limit Level			
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A)/ 70 dB(A)/ 65 dB(A) ^{Note 1}			

Note 1:

- 70dB(A) and 65 dB(A) for schools during normal teaching periods and school examination periods, respectively.

If works are to be carried out during the restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

Action and Limit Level for Air Quality Monitoring

Monitoring Location	1-hour TSP Level	in μ g/m ³	24-hour TSP Level in μ g/m ³				
	Action Level	Limit Level	Action Level	Limit Level			
CMA1b	320.1	500	176.7	260			
CMA2a	323.4	500	169.5	260			
CMA3 a	311.3	500	171.0	260			
CMA4a	312.5	500	171.2	260			
CMA5b	332.0	500	181.0	260			
MA1e	325.1	500	173.4	260			
MA1w	325.1	500	173.4	260			



Appendix 4.2

Copies of Calibration Certificates

15	60	21-			6		D	ALIBRATION
_					2		Janua	ary 24, 201
nvir	onm	ent	al	-				
•	Ce	rtifa	cate of		Cal	ibri	ntion	
			Calibration (Certificatio	n Informat	ion		
Cal. Date:	January 24	2018	Rootsr	neter S/N:	438320	Tav	293	°K
Operator:	Jim Tisch	V1251			450520			1.2.92
		10.20 II 40.30 M				Pa:	756.9	mm Hg
Calibration	Model #:	TE-5025A	Calib	rator S/N:	3166			
		Vol. Init	Vol. Final	ΔVol.	ΔTime	40		1
	Run	(m3)	(m3)			ΔP	ΔH	
	1	1	(113)	(m3) 1	(min) 1.4430	(mm Hg)	(in H2O)	-
	2	3	4	1	1.0270	3.2	2.00	-
	3	5	6	1	0.9220	7.9	5.00	· · ·
	4	7	8	1	0.8780	8.7	5.50	
	5	9	10	1	0.7270	12.6	8.00	
						12.0	0.00]
			D	ata Tabulat	ion			
	Vstd	Qstd	$\sqrt{\Delta H \left(\frac{Pa}{Pstd}\right)}$)(<u>Tstd</u>)		Qa	√∆н(та/Ра)	
	(m3)	(x-axis)	(y-axi	s)	Va	(x-axis)	(y-axis)	
	1.0087	0.6990	1.423	3	0.9958	0.6901	0.8799	
	1.0044	0.9780	2.012		0.9915	0.9655	1.2443	
	1.0024	1.0872	2.250		0.9896	1.0733	1.3912	
	1.0013	1.1404	2.360		0.9885	1.1259	1.4591	-
	0.9961	1.3701	2.846		0.9834	1.3526	1.7598	
	OCTO		2.122			m=	1.32895	
	QSTD	b=	-0.060		QA [b=	-0.03719	
		r=	0.9999	99		r=	0.99999	
				Calculation	s			1
	Vstd=	ΔVol((Pa-ΔP)	/Pstd)(Tstd/Ta)	Va=	ΔVol((Pa-ΔF	P)/Pa)	
	Qstd=	Vstd/∆Time			Qa=	Va/∆Time		
			For subseque	ent flow rat	e calculation	IS:		
	Qstd=	1/m ((\\ \ \ \ \ \ \ \ \ \ (Pa (Tstd Pstd (Ta))-b)	Qa=	1/m ((√∆H	(Ta/Pa))-b)	
	Standard	Conditions						La la companya di seconda di s
Tstd:	298.15			Г		RECAL	IBRATION	
Pstd:		nm Hg		H				
		ey					nual recalibratio	
		er reading (in					egulations Part 5	
ΔP: rootsme	ter manome	ter reading (mm Hg)				Reference Meth	
	Southe temp	erature ("K)			Dotorminati	on of Surn	ended Particulate	Adattar in
Ta: actual ab Pa: actual ba			49)				re, 9.2.17, page 3	Contraction of the second s

Tisch Environmental, Inc. 145 South Miami Avenue



Location	:	CMA1b	Calibration Date	:	23-Aug-18
Equipment no.	:	HVS001	Calibration Due Date	:	23-Oct-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition									
Temperature, T _a		300.7	7	Kelvin	Kelvin Pressure, P _a 1011 mmHg				
			Orifice	Transfer Sta	ndard Inform	ation			
Equipment No.		Ori002		Slope, m _c	2.122	31	Intercept, bc	-0.06016	
Last Calibration Date		19-Jan-18	8		(H	x P _a / 10)13.3 x 298 / T	a) ^{1/2}	
Next Calibration Date		19-Jan-19	9			m _c	x Q _{std} + b _c		
				Calibratio	n of TSP				
Calibration	Mai	nometer Re	eading	a	std	Conti	nuous Flow	IC	
Point	Н ((inches of v	water)	(m ³ / min.)		Red	corder, W	$(W(P_a/1013.3x298/T_a)^{1/2}/35.31)$	
	(up)	(down)	(difference)	X-4	axis		(CFM)	Y-axis	
1	1.5	1.5	3.0	0.8	397		24	23.8602	
2	2.5	2.5	5.0	1.0	758		32	31.8135	
3	3.9	3.9	7.8	1.3	366		42	41.7553	
4	5.0	5.0	10.0	1.5	6097		48	47.7203	
5	6.1	6.1	12.2	1.6	645		53	52.6912	
By Linear Regression of Y o	on X								
	Slope, m	=	35.:	3840		tercept, b =	-5.9	9099	
Correlation C	oefficient*	=	0.9	9996	_				
Calibration	Accepted	=	Yes	:/ No **	_				

 * if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been

re-ass	signed from	EL452 to HVS001 with res	pect to the update in quality management system.		
Calibrated by	:	Ray Lee	Checked by	:	Pauline Wong
Date	:	23-Aug-18	Date	:	23-Aug-18



Location	:	CMA2a	Calibration Date	:	23-Aug-18
Equipment no.	:	HVS002	Calibration Due Date	:	23-Oct-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition									
Temperature, T _a		300.7	7	Kelvin	Pressure, P _a	1	10)11 mmHg	
			Orifice	Transfer Sta	andard Inform	ation			
Equipment No.		Ori002		Slope, m _c	2.122	31	Intercept, bc	-0.06016	
Last Calibration Date		19-Jan-18	8		(H	x P _a / 10	013.3 x 298 / T	(a) ^{1/2}	
Next Calibration Date		19-Jan-19	9			m _c	x Q _{std} + b _c		
				Calibratio	n of TSP				
Calibration	Mai	nometer Re	eading	G	Q _{std}	Conti	nuous Flow	IC	
Point	н ((inches of v	water)	(m ³ / min.)		Red	corder, W	$(W(P_a/1013.3x298/T_a)^{1/2}/35.31)$	
	(up)	(down)	(difference)	X -6	axis		(CFM)	Y-axis	
1	1.6	1.6	3.2	0.8	8663		28	27.8368	
2	2.2	2.2	4.4	1.(0110		35	34.7961	
3	3.7	3.7	7.4	1.8	3026		44	43.7436	
4	4.6	4.6	9.2	1.4	4492		51	50.7028	
5	5.9	5.9	11.8	1.6	6375		54	53.6854	
By Linear Regression of Y o	ın X								
	Slope, m	=	34.	0314	Int	tercept, b =	-0.4	1992	
Correlation C	oefficient*	=	0.9	9914	_				
Calibration	Accepted	=	Yes	s/ No **	_				

 * if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been

<u>re-ass</u>	igned from	EL449 to HVS002 with res	pect to the update in quality management system.		
Calibrated by	:	Ray Lee	Checked by	:	Pualine Wong
Date	:	23-Aug-18	Date	:	23-Aug-18



Location Equipment no. CMA3a HVS012

Calibration Date	:
Calibration Due Date	:

23-Aug-18 23-Oct-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition									
Temperature, T _a	rature, T _a 300.7 Kelvin Pressure, P _a 1011 mmHg								
Orifice Transfer Standard Information									
Equipment No.	Ori002	Slope, m _c	2.12231	Intercept, bc	-0.06016				
Last Calibration Date	19-Jan-18	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$							
Next Calibration Date	19-Jan-19	$m_{c} \times Q_{std} + b_{c}$							
		Calibration	of TSP						
Calibration	Manometer Reading	Q	std Cor	ntinuous Flow	IC				
Point	H (inches of water)	(m ³ /	min.) F	Recorder, W	$(W(P_a/1013.3x298/T_a)^{1/2}/35.31)$				
	(up) (down) (difference)	¥-2	vie	(CEM)	V-avie				

	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis
1	1.3	1.3	2.6	0.7837	28	27.8368
2	2.3	2.3	4.6	1.0330	35	34.7961
3	3.2	3.2	6.4	1.2134	41	40.7611
4	4.2	4.2	8.4	1.3860	47	46.7261
5	5.4	5.4	10.8	1.5678	52	51.6970
By Linear Regression of Y	on X					
Slope, m		=	30.9	9858 Int	tercept, b =	3.2800
Correlation Coefficient*		=	0.99	991		
Calibration	Accepted	=	Yes/	No**		

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been

re-assigned from FI	L333 to HVS012 with respect	t to the undate in quality ma	nagement system
To assigned north El		t to the apparte in quality int	anagoment system.

Calibrated by	:	Ray Lee	Checked by	:	Pauline Wong
Date	:	23-Aug-18	Date	: _	23-Aug-18



Location Equipment no. CMA4a HVS004 Calibration Date Calibration Due Date 23-Aug-18 23-Oct-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition									
Temperature, T _a	300.7	Kelvin	Pressure, P _a	1011	mmHg				
Orifice Transfer Standard Information									
Equipment No.	Ori002	Slope, m _c	2.12231	Intercept, bc	-0.06016				
Last Calibration Date	19-Jan-18	$(H x P_a / 1013.3 x 298 / T_a)^{1/2}$							
Next Calibration Date	19-Jan-19		$m_{c} \times Q_{std} + b_{c}$						

				Calibration of TSP		
Calibration	Calibration Manon		eading	Q _{std}	Continuous Flow	IC
Point	Н (inches of v	water)	(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.3
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis
1	1.4	1.4	2.8	0.8122	22	21.8718
2	2.0	2.0	4.0	0.9652	29	28.8310
3	3.6	3.6	7.2	1.2853	42	41.7553
4	4.7	4.7	9.4	1.4646	48	47.7203
5	5.8	5.8	11.6	1.6238	54	53.6854
near Regression of	Y on X	<u>.</u>				
	Slope, m	=	38.	9454 I	ntercept, b =	-9.1384
Correlation	Coefficient*	=	0.9	990		
Calibratio	n Accepted	=	Yes	/ No **		

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks :	As per client's provided information,	the equipment reference no. of	the calibrated High	Volume Sampler has been
-----------	---------------------------------------	--------------------------------	---------------------	-------------------------

 re-assigned from EL390 to HVS004 with respect to the update in quality management system.

 Calibrated by
 :
 Ray Lee
 Checked by
 :
 Pauline Wong

 calibrated by
 :
 23-Aug-18
 Date
 :
 23-Aug-18

Date



Location Equipment no. CMA5b HVS010

Calibration Date	
Calibration Due Date	

23-Aug-18 23-Oct-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

				Ambient C						
Temperature, T _a		300.	7	Kelvin	Pressure, P _a		10)11	mmHg	
	Orifice Transfer Standard Information									
Equipment No.		Ori002		Slope, m _c	2.1223		Intercept, bc	-0.0	6016	
Last Calibration Date		19-Jan-1	8		(H	x P _a / 1	013.3 x 298 / 1	$(\Gamma_{a})^{1/2}$		
Next Calibration Date		19-Jan-1	9		=	m _c	$x Q_{std} + b_{c}$			
	Calibration of TSP									
Calibration	Ma	nometer Re	eading	Q	std	Cont	inuous Flow	IC	;	
Point	H (inches of v	water)	(m ³ /	min.)	Re	ecorder, W	(W(P _a /1013.3x29	98/T _a) ^{1/2} /35.31)	
	(up)	(down)	(difference)	X-a	axis		(CFM)	Y-ax	ris	
1	1.5	1.5	3.0	0.8	397		34	33.80)19	
2	2.1	2.1	4.2	0.9	884		40	39.76	69	
3	3.4	3.4	6.8	1.2	499		48	47.72	203	
4	4.4	4.4	8.8	1.4	180		54	53.68	354	
5	5.6	5.6	11.2	1.5	960		59	58.65	562	
By Linear Regression of Y o	n X									
	Slope, m	=	32.7	7067	Int	ercept, b	= 6.8	3765		
Correlation C	oefficient*	=	0.9	988	-				_	
Calibration	Accepted	=	Yes	/ No **	-					
L										

* if Correlation Coefficient < 0.990, check and recalibration again.

** Delete as appropriate.

Remarks : As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been

re-assigned from EL222 to HVS010 with respect to the update in quality management system.

Calibrated by Date Ray Lee 23-Aug-18 Checked by Date



Location Equipment no. CMA6a HVS013

Calibration Date	:	23-Ai
Calibration Due Date	:	23-0

23-Aug-18 23-Oct-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

				Ambient Co						
Temperature, T _a		300.7 Kelvin Pressure, P a 1011 mmHg								
Orifice Transfer Standard Information										
Equipment No.		Ori002		Slope, m _c	2.1223	1	Intercept, bc	-0.06016		
Last Calibration Date		19-Jan-1	8		(H)	x P _a / 10	13.3 x 298 / T	a) ^{1/2}		
Next Calibration Date		19-Jan-1	9		=	m _c >	k Q _{std} + b _c			
				Calibration	of TSP					
Calibration	Mai	nometer Re	eading	Q	std	Contir	nuous Flow	IC		
Point	Н (inches of v	vater)	(m ³ /	min.)	Rec	order, W	$(W(P_a/1013.3x298/T_a)^{1/2}/35.31)$		
	(up)	(down)	(difference)	X-a	xis	((CFM)	Y-axis		
1	1.5	1.5	3.0	0.8	397		32	31.8135		
2	2.3	2.3	4.6	1.0	330		39	38.7728		
3	3.3	3.3	6.6	1.2	318		44	43.7436		
4	4.4	4.4	8.8	1.4	180		50	49.7087		
5	4.9	4.9	9.8	1.4	948		54	53.6854		
By Linear Regression of Y o	n X	<u>.</u>								
	Slope, m	=	31.9	490	Inte	ercept, b =	5.09	55		
Correlation C	oefficient*	=	0.99	965						
Calibration	Accepted	=	Yes/	No**						

* if Correlation Coefficient < 0.990, check and recalibration again.

:

:

** Delete as appropriate.

 Remarks :
 As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been

 re-assigned from EL551 to HVS013 with respect to the update in quality management system.

Calibrated by Date Ray Lee 23-Aug-18 Checked by Date



Location Equipment no. MA1e HVS007 Calibration Date Calibration Due Date

23-Aug-18 23-Oct-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

Temperature, T _a		300.	7	Kelvin Pressu	ire P	1	011 mmHg	
		500.	7	Reivin ressu	ile, r _a	1	un mining	
			Orifice Tr	ansfer Standard Ir	formation			
Equipment No.		Ori002		Slope, m _c 2	.12231	Intercept, bc	-0.06016	
Last Calibration Date		19-Jan-1	8	(H x P _a / 1	013.3 x 298 / [·]	T _a) ^{1/2}	
Next Calibration Date		19-Jan-1	9		m _c	$x Q_{std} + b_{c}$		
				Calibration of TSF	b			
Calibration	Ма	Manometer Reading Q std Continuous Flow IC					IC	
Point	H (inches of water)		(m ³ / min.) Recorder, W (W(P _a /1013.3x298					
	(up)	(down)	(difference)	X-axis	X-axis (CFI		Y-axis	
1	1.5	1.5	3.0	0.8397		24	23.8602	
2	2.2	2.2	4.4	1.0110		32	31.8135	
3	3.6	3.6	7.2	1.2853		44	43.7436	
4	4.7	4.7	9.4	1.4646		51	50.7028	
5	5.7	5.7	11.4	1.6100 56 55.6737				

 Slope, m
 =
 41.5273
 Intercept, b
 =
 -10.4222

 Correlation Coefficient*
 =
 0.9988

 Calibration Accepted
 =
 Yes/Ne**

* if Correlation Coefficient < 0.990, check and recalibration again.

Remarks : As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been re-assigned from EL455 to HVS007 with respect to the update in quality management system.

Calibrated by Date Ray Lee 23-Aug-18 Checked by Date



Location Equipment no. MA1w HVS008 Calibration Date Calibration Due Date

23-Aug-18 23-Oct-18

CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition									
Temperature, T _a	300.7	Kelvin	Pressure, P _a	10	11 mmHg				
	Orifice 1	ransfer Stan	ndard Information						
Equipment No.	Ori002	Slope, m _c	2.12231	Intercept, bc	-0.06016				
Last Calibration Date	19-Jan-18		(H x P _a / 10	013.3 x 298 / T	a) ^{1/2}				
Next Calibration Date	19-Jan-19		= m _c	x Q _{std} + b _c					

				Calibration of TSP			
Calibration	Calibration Mano		Manometer Reading		Continuous Flow	IC	
Point	н	inches of	water)	(m ³ / min.)	Recorder, W	(W(P _a /1013.3x298/T _a) ^{1/2} /35.31	
	(up)	(down)	(difference)	X-axis	(CFM)	Y-axis	
1	1.5	1.5	3.0	0.8397	20	19.8835	
2	2.4	2.4	4.8	1.0546	27	26.8427	
3	3.6	3.6	7.2	1.2853	36	35.7902	
4	5.0	5.0	10.0	1.5097	42	41.7553	
5	6.4	6.4	12.8	1.7043	50	49.7087	
y Linear Regression of	Y on X				•		
	Slope, m	=	34.1	180 l	ntercept, b =	-8.8315	
Correlation	Coefficient*	=	0.99	985			
Calibratio	on Accepted	=	Yes/	\o **			

* if Correlation Coefficient < 0.990, check and recalibration again.

 Remarks :
 As per client's provided information, the equipment reference no. of the calibrated High Volume Sampler has been re-assigned from EL080 to HVS008 with respect to the update in quality management system.

Calibrated by Date Ray Lee 23-Aug-18 Checked by : ____ Date : ____



综合試驗 有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website; www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:	18CA0322 01		Page	1	of 2	2
Item tested						
Description: Manufacturer: Type/Model No.: Serial/Equipment No.: Adaptors used:	Sound Level Meter (Larson Davis LxT1 0003737	Type 1)	Microphone PCB 377B02 171529 -			
Item submitted by						
Customer Name: Address of Customer: Request No.: Date of receipt:	Lam Geotechnics Lte - 22-Mar-2018	d.				
Date of test:	28-Mar-2018					
Reference equipment	used in the calibra	tion				
Description: Multi function sound calibrator Signal generator	Model: B&K 4226 DS 360	Serial No. 2288444 61227	Expiry Date: 08-Sep-2018 01-Apr-2018		Traceable (CIGISMEC CEPREI	to:
Ambient conditions						
Temperature:	21 ± 1 °C					

Test specifications

Relative humidity:

Air pressure:

- The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of +20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.


Actual Measurement data are documented on worksheets.

Approved Signatory:



50 ± 10 %

1005 ± 5 hPa





Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

Date:

© Soils & Materials Engineering Co. Ltd.

Form No CARP152-1/Issue 1/Rev C/01/02/2007



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

·港黄竹坑道37號利達中心12樓

12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



2

CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA0322 01

Page 2 of

1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
(1) 4 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	c	Pass	0.8	2.1
	Lin	Pass	1.6	2.2
Linearity range for Leg	At reference range , Step 5 dB at 4 kHz	Pass	0.3	2.2
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	지수는 모양은 방법에 가지 않는 것 같은 것 같	Pass	0.3	
	AC	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	N/A	N/A	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 ³ at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	5-20 S	
Pulse range		50.00555	0.3	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

2, Acoustic tests


The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz Weighting A at 8000 Hz	Pass Pass	0.3 0.5	

Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.



The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

C Soils & Materials Engineering Co. Ltd.

Form No CARP 152-2/Issue 1/Rev C/01/02/2007



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 港 黃 竹 坑 道 3 7 號 利 達 中 心 1 2 樓 香

12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:	18CA0213 02		Page	1 of	2
Item tested					
Description: Manufacturer: Type/Model No.: Serial/Equipment No.: Adaptors used:	Sound Level Me B & K 2250 2701778 -	ter (Type 1)	Microphone B & K 4950 2755097	Preamp B & K ZC0032 19223 -	
Item submitted by					
Customer Name: Address of Customer: Request No.: Date of receipt:	Lam Geotechnic - - 13-Feb-2018	s Limited.			
Date of test:	21-Feb-2018				
Reference equipment	used in the cal	bration			
Description: Multi function sound calibrator	Model: B&K 4225	Serial No. 2288444	Expiry Date: 08-Sep-2018	Traceab CIGISME	10000

Multi function sound calibrator	B&K 4226	2288444	08-Sep-2018	CIGISME
Signal generator	DS 360	33873	25-Apr-2018	CEPREI
Signal generator	DS 360	61227	01-Apr-2018	CEPREI
Ambient conditions				

Temperature:	20 ± 1 °C
Relative humidity:	50 ± 10 %
Air pressure:	1000 ± 5 hPa

Test specifications

- 1. The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580; Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- 2. The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of +20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference 3. between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets

Approved Signatory: Fen Jun 0

21-Feb-2018 Company Chop:



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

Date:

C Soils & Materials Engineering Co. Ltd

Form No CARP152-Missue 1/Rev C/01/02/2007



综合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港黄竹坑道 37號利達中心12樓

12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website; www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA0213 02

Page

2 of 2

1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

			Expanded	Coverage
Test:	Subtest:	Status:	Uncertanity (dB)	Factor
Self-generated noise	А	Pass	0.3	
	c	Pass	0.8	
	Lin	Pass	1.6	
Linearity range for Leq	At reference range, Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	A	Pass	0.3	
	C	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 ³ at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz	Pass	0.3	
	Weighting A at 8000 Hz	Pass	0.5	

3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.



The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

C Soils & Material's Engineering Co. Ltd

Form No CARP152-2/Issue 1/Rev C/01/02/2007



综合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Certificate No.:	18CA0309 01		Page	1	of	2
Item tested						
Description: Manufacturer: Type/Model No.: Serial/Equipment No.: Adaptors used:	Sound Level Mete B & K 2250-L 2722310	r (Type 1)	Microphone B & K 4950 2698702		Preamp B & K ZC0032 13318	
Item submitted by						
Customer Name: Address of Customer: Request No.: Date of receipt:	Lam Geotechnics - - 09-Mar-2018	Ltd.				
Date of test:	10-Mar-2018					
Reference equipment	used in the calib	ration				
Description: Multi function sound calibrator Signal generator Signal generator	Model: B&K 4226 DS 360 DS 360	Serial No. 2288444 33873 61227	Expiry Date: 08-Sep-2018 25-Apr-2018 01-Apr-2018		Traceab CIGISME CEPREI CEPREI	ST
Ambient conditions						
Temperature: Relative humidity: Air pressure:	21 ± 1 °C 50 ± 10 % 1000 ± 5 hPa					
Test specifications						

- The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.

Approved Signatory: Date: 12-Mar-2018 Company Chop:

Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

© Soils & Materials Engineering Co. Ltd.

Form No CARP152-1/Issue 1/Rev C/01/02/2007



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

香港黄竹坑道37號利達中心12樓

12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong. E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



Causana

CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA0309 01

Page

2 of 2

Europedad

1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	A	Pass	0.3	
5	C	Pass	0.8	
	Lin	Pass	1.6	
Linearity range for Leq	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
150 TH 50	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	A	Pass	0.3	
	C	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
CONCERNMENT CONTRACTOR	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/103 at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

2, Acoustic tests


The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Weighting A at 125 Hz	Pass	0.3	
		Weighting A at 125 Hz Pass	Subtest Status Uncertanity (dB) Weighting A at 125 Hz Pass 0.3

3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.



The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co. Ltd.

Form No CARP152-2/Issue 1/Rev C/01/02/2007



余字合試験有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港黄竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.

E-mail: smec@cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Website: www.cigismec.com

Certificate No.:	18CA0413 02		Page	1 of	2
Item tested					
Description:	Sound Level Met	ter (Type 1)	Microphone	Pream	p
Manufacturer:	B & K		B&K	8 & K	
Type/Model No.:	2250-L		4950	ZC003	2
Serial/Equipment No.:	2722311		2698703	13321	
Adaptors used:			(5)	57	
Item submitted by					
Customer Name:	Lam Geotechnic	s Ltd.			
Address of Customer:	. F.				
Request No.:	-				
Date of receipt:	13-Apr-2018				
Date of test:	18-Apr-2018				
Reference equipment	used in the cali	bration			
Description:	Model:	Serial No.	Expiry Date:	Tracea	able to:
Multi function sound calibrator	B&K 4226	2288444	08-Sep-2018	CIGISM	IEC
			25-Apr-2018	CEPRE	

Ambient conditions

Temperature:	20 ± 1 °C
Relative humidity:	50 ± 10 %
Air pressure:	1000 ± 5 hPa

Test specifications

- The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580: Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580: Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Actual Measurement data are documented on worksheets.



Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

© Soits & Materials Engineering Co. Ltd.

Form No CARP152-1/Issue 1/Rev C/01/02/2007



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港首竹坑道37號利達中心12樓

12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong, E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA0413 02

```
Page 2
```

2 of 2

1, Electrical Tests

The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	А	Pass	0.3	
	C	Pass	0.8	
	Lin	Pass	1.6	
Linearity range for Leg	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
10 A B	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	A	Pass	0.3	
	С	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 ³ at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

2, Acoustic tests


The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz Weighting A at 8000 Hz	Pass Pass	0.3	

3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.



The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

C Soils & Materials Engineering Co. Ltd

Form No.CARP152-2/Issue 1/Rev C/01/02/2007





CERTIFICATE OF CALIBRATION

Certificate No.:	18CA0116 01		Page	1	of	2
Item tested						
Description: Manufacturer: Type/Model No.: Serial/Equipment No.: Adaptors used:	Sound Level Mete B & K 22501. 3002695	er (Type 1)	Microphone B & K 4950 2940839		Preamp B & K ZC0032 18582	
Item submitted by						
Customer Name: Address of Customer: Request No.: Date of receipt:	Lam Geotechnics - - 16-Jan-2018	Ltd.				
Date of test:	18-Jan-2018					
Reference equipment	used in the calib	ration				
Description: Multi function sound calibrator Signal generator Signal generator	Model: B&K 4226 DS 360 DS 360	Serial No. 2268444 33873 61227	Expiry Date: 08-Sep-2018 25-Apr-2018 01-Apr-2018		Traceabl CIGISMEC CEPREI CEPREI	
Ambient conditions						
Temperature: Relative humidity:	21 ± 1 °C 50 ± 10 %					

Test specifications

Air pressure:

- The Sound Level Meter has been calibrated in accordance with the requirements as specified in BS 7580. Part 1: 1997 and the lab calibration procedure SMTP004-CA-152.
- The electrical tests were performed using an electrical signal substituted for the microphone which was removed and replaced by an equivalent capacitance within a tolerance of ±20%.
- The acoustic calibration was performed using an B&K 4226 sound calibrator and corrections was applied for the difference between the free-field and pressure responsess of the Sound Level Meter.

Test results

This is to certify that the Sound Level Meter conforms to BS 7580; Part 1: 1997 for the conditions under which the test was performed.

Details of the performed measurements are presented on page 2 of this certificate.

Feng Jun Qi

1005 ± 5 hPa

Actual Measurement data are documented on worksheets.

Approved Signatory:

18-Jan-2018 Company Chop:



Comments: The results reported in his certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long-term stability of the instrument.

Date:

C Sols & Materials Engineering Co. Ltd

Form No CARP152-1/Issue 1/Rev C/01/02/2007

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. HOKLAS 028 - CAL) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation. Such terms of accreditation stipulate that the results shall be traceable to the International System of Units (S.I.) or recognised measurement standards. This certificate shall not be reproduced except in full.



綜合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港黃竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.

E-mail: smec@cigismec.com Website: www.cigismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



2

CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA0116 01

Page of

1, **Electrical Tests**

> The electrical tests were performed using an equivalent capacitance substituted for the microphone. The results are given in below with test status and the estimated uncertainties. The "Pass" means the result of the test is inside the tolerances stated in the test specifications. The "-" means the result of test is outside these tolerances.

Test:	Subtest:	Status:	Expanded Uncertanity (dB)	Coverage Factor
Self-generated noise	А	Pass	0.3	
	C	Pass	0.8	
	Lin	Pass	1.6	
Linearity range for Leq	At reference range , Step 5 dB at 4 kHz	Pass	0.3	
	Reference SPL on all other ranges	Pass	0.3	
	2 dB below upper limit of each range	Pass	0.3	
	2 dB above lower limit of each range	Pass	0.3	
Linearity range for SPL	At reference range . Step 5 dB at 4 kHz	Pass	0.3	
Frequency weightings	A	Pass	0.3	
	C	Pass	0.3	
	Lin	Pass	0.3	
Time weightings	Single Burst Fast	Pass	0.3	
	Single Burst Slow	Pass	0.3	
Peak response	Single 100µs rectangular pulse	Pass	0.3	
R.M.S. accuracy	Crest factor of 3	Pass	0.3	
Time weighting I	Single burst 5 ms at 2000 Hz	Pass	0.3	
	Repeated at frequency of 100 Hz	Pass	0.3	
Time averaging	1 ms burst duty factor 1/10 ³ at 4kHz	Pass	0.3	
	1 ms burst duty factor 1/10 ⁴ at 4kHz	Pass	0.3	
Pulse range	Single burst 10 ms at 4 kHz	Pass	0.4	
Sound exposure level	Single burst 10 ms at 4 kHz	Pass	0.4	
Overload indication	SPL	Pass	0.3	
	Leq	Pass	0.4	

2, Acoustic tests

The complete sound level meter was calibrated on the reference range using a B&K 4226 acoustic calibrator with 1000Hz and SPL 94 dB. The sensitivity of the sound level meter was adjusted. The test result at 125 Hz and 8000 Hz are given in below with test status and the estimated uncertainties.

Test:	Subtest	Status	Expanded Uncertanity (dB)	Coverage Factor
Acoustic response	Weighting A at 125 Hz Weighting A at 8000 Hz	Pass Pass	0.3 0.5	

3, Response to associated sound calibrator

N/A

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

		- End -	1	
Calibrated by:	11	Checked by:	K	
Date:	Fung Chi Yip	Date:	Lam Tze Wai 18-Jan-2018	

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

C Soils & Materials Engineering Co.: Ltd.

Form No CARP152-2/Issue 1/Rev C/01/02/2007

Hong Kong Accreditation Service (HKAS) has accredited this laboratory (Reg. No. HOKLAS 028 - CAL) under the Hong Kong Laboratory Accreditation Scheme (HOKLAS) for specific calibration activities as listed in the HOKLAS Directory of Accredited Laboratories. The results shown in this certificate were determined by this laboratory in accordance with its terms of accreditation. Such terms of accreditation stipulate that the results shall be traceable to the International System of Units (S.I.) or recognised measurement standards. This certificate shall not be reproduced except in full.



综合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD. 香港黃竹坑道37號利達中心12樓 12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong.

E-mail: smec@clgismec.com

Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

Website: www.cigismec.com

Certificate No.:	18CA0309 02	Page: 1	of	2	
Item tested					
Description:	Acoustical Calibrator (Class 1)				
Manufacturer:	Larson Davis				
Type/Model No.:	CAL200				
Serial/Equipment No.:	13098				
Adaptors used:	5				
Item submitted by					
Curstomer:	Lam Environmental Service Ltd.				
Address of Customer:	-				
Request No.:					
Date of receipt:	09-Mar-2018				
Date of test:	12-Mar-2018				

Reference equipment used in the calibration

Description:	Model:	Serial No.	Expiry Date:	Traceable to:
Lab standard microphone	B&K 4180	2341427	11-Apr-2018	SCL
Preamplifier	B&K 2673	2239857	05-May-2018	CEPREI
Measuring amplifier	B&K 2610	2346941	03-May-2018	CEPREI
Signal generator	DS 360	61227	01-Apr-2018	CEPREI
Digital multi-meter	34401A	US36087050	25-Apr-2018	CEPREI
Audio analyzer	8903B	GB41300350	21-Apr-2018	CEPREI
Universal counter	53132A	MY40003662	22-Apr-2018	CEPREI

Ambient conditions

Temperature:	21 ± 1 °C
Relative humidity:	50 ± 10 %
Air pressure:	1000 ± 5 hPa

Test specifications

- The Sound Calibrator has been calibrated in accordance with the requirements as specified in IEC 60942 1997 Annex B and the lab calibration procedure SMTP004-CA-156.
- The calibrator was tested with its axis vertical facing downwards at the specific frequency using insert voltage technique.
- The results are rounded to the nearest 0.01 dB and 0.1 Hz and have not been corrected for variations from a reference pressure of 1013.25 hectoPascals as the maker's information indicates that the instrument is insensitive to pressure changes.

Test results

This is to certify that the sound calibrator conforms to the requirements of annex B of IEC 60942 (1997 for the conditions under which the test was performed. This does not imply that the sound calibrator meets IEC 60942 under any other conditions.

Details of the performed measurements are presented on page 2 of this certificate.



Approved Signatory:

n Fenal Jun O

12-Mar-2018 Company Chop:

Comments: The results reported in this certificate refer to the condition of the instrument on the date of calibration and carry no implication regarding the long term stability of the instrument.

Date:

© Soils & Materials Engineering Co., Ltd.

Form No. CARP155-1/Issue 1/Rev. 0/01/03/2007



综合試驗有限公司 SOILS & MATERIALS ENGINEERING CO., LTD.

下港 黃 竹 坑 道 3 7 號 利 逵 中 心 1 2 樓

12/F., Leader Centre, 37 Wong Chuk Hang Road, Aberdeen, Hong Kong, E-mail: smec@cigismec.com Website: www.cigismec.com Tel: (852) 2873 6860 Fax: (852) 2555 7533



CERTIFICATE OF CALIBRATION

(Continuation Page)

Certificate No.:

18CA0309 02

Page: 2 of 2

1, Measured Sound Pressure Level

The output Sound Pressure Level in the calibrator head was measured at the setting and frequency shown using a calibrated laboratory standard microphone and insert voltage technique. The results are given in below with the estimated uncertainties.

			(Output level in dB re 20 µPa
Frequency Shown Hz	Output Sound Pressure Level Setting dB	Measured Output Sound Pressure Level dB	Estimated Expanded Uncertainty dB
1000	94.0	93.81	0.10

2, Sound Pressure Level Stability - Short Term Fluctuations

The Short Term Fluctuations was determined by measuring the maximum and minimum of the fast weighted DC output of the B&K 2610 measuring amplifier over a 20 second time interval as required in the standard. The Short Term Fluctuation was found to be

At 1000 Hz	STF = 0.011 dB
Estimated expanded uncertainty	0.005 dB

3, Actual Output Frequency

The determination of actual output frequency was made using a B&K 4180 microphone together with a B&K 2673 preamplifier connected to a B&K 2610 measuring amplifier. The AC output of the B&K 2610 was taken to an universal counter which was used to determine the frequency averaged over 20 second of operation as required by the standard. The actual output frequency at 1 KHz was:

At 1000 Hz	Actual Frequency = 1000.0 Hz	
Estimated expanded uncertainty	0.1 Hz	Coverage factor k = 2 2

4, Total Noise and Distortion

For the Total Noise and Distortion measurement, the unfiltered AC output of the B&K 2610 measuring amplifier was connected to an Agilent Type 8903 B distortion analyser. The TND result at 1 KHz was:

At 1000 Hz	TND = 0.6 %
Estimated expanded uncertainty	0.7 %

The expanded uncertainties have been calculated in accordance with the ISO Publication "Guide to the expression of uncertainty in measurement", and gives an interval estimated to have a level of confidence of 95%. A coverage factor of 2 is assumed unless explicitly stated.

	4	- End -		
Calibrated by:	1~~(Checked by:	F	
Date:	Fung Chi Yip 12-Mar-2018	Date:	Lam Tze Wai 12-Mar-2018	

The standard(s) and equipment used in the calibration are traceable to national or international recognised standards and are calibrated on a schedule to maintain the required accuracy level.

© Soils & Materials Engineering Co. Ltd



Appendix 5.1

Monitoring Schedules for Reporting Month and Coming Reporting Month

Contract No. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3) Tentative Environmental Monitoring Schedule September 2018

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	27-Aug	28-Aug	29-Aug	30-Aug	31-Aug	1-Sep
		24hr TSP (CMA5b, MA1e) 1hr TSP		Noise (daytime) (M3a, M4b)	Noise (daytime) (M1a, M2b, M5b, M6)	24hr TSP (CMA1b, CMA2a, CMA3a, CMA4a, CMA5b, MA1w)
2-Sep	3-Sep	4-Sep	5-Sep	6-Sep	7-Sep	8-Sep
	24hr TSP (MA1e) 1hr TSP	Noise (daytime) (M3a, M4b, M7e, M7w, M8)	Noise (daytime) (M1a, M2b, M5b, M6)		24hr TSP	1hr TSP
9-Sep	10-Sep	11-Sep	12-Sep	13-Sep	14-Sep	15-Sep
		Noise (daytime) (M3a, M4b, M5b, M6, M7e, M7w, M8)	24hr TSP Noise (daytime) (M1a, M2b)	1hr TSP	
16-Sep) 17-Sep	18-Sep	19-Sep	20-Sep	21-Sep	22-Sep
		Noise (daytime) (M7e, M7w, M8)			Noise (daytime) (M1a, M2b, M3a, M4b, M5b, M6)	
23-Sep	24-Sep	25-Sep	26-Sep	27-Sep		
	24hr TSP (CMA1b, CMA2a, CMA4a, CMA5b, MA1e, MA1w) Noise (daytime) (M7e, M7w, M8)		24hr TSP (CMA3a) 1hr TSP Noise (daytime) (M1a)	Noise (daytime) (M2b, M3a, M4b, M5b, M6)		

Contract No. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3) Tentative Environmental Monitoring Schedule October 2018

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				27-Sep	28-Sep	29-Sep
						24hr TSP
30-Sep	1-Oct	2-Oct	3-Oct	4-Oct	5-Oct	6-Oct
		1hr TSP			24hr TSP	1hr TSP
		Noise (daytime)	Noise (daytime)			
7-Oct	t 8-Oct	9-Oct	10-Oct	11-Oct	12-Oct	13-Oct
				24hr TSP	1hr TSP	
	Noise (daytime)	Noise (daytime)				
14-Oct	t 15-Oct	16-Oct	17-Oct	18-Oct	19-Oct	20-Oct
	Noise (daytime)	24hr TSP Noise (daytime)		1hr TSP		
	Noise (dayume)	Noise (uzyuine)				
21-Oct	t 22-Oct	23-Oct	24-Oct	25-Oci	26-Oct	
21-00	22-Oct	23-Uct	24-Oct	25-00	26-Uct	
	24hr TSP	1hr TSP				



Appendix 5.2

Noise Monitoring Results and Graphical Presentations



Day Time (0700 - 1900hrs on normal weekdays)

Location: M1a - Footbridge at EX-Wanchai Harbour Road Sports Centre

			Measur	ement Noi	se Level	Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq	Leq L10		Leq	Leq	Leq
					Unit: dB	(A), (30-min)		
31/8/18	13:00	Cloudy	70.9	70.9 73.9 66.3		72	71	75
5/9/18	11:07	Fine	72.8	75.3	68.4	72	64	75
13/9/18	10:50	Cloudy	65.9	68.3	62.6	72	66	75
21/9/18	14:30	Fine	71.4 74.2 66.5		66.5	72	71	75
26/9/18	11:05	Fine	71.0 73.7 66.1		72	71	75	



Day Time (0700 - 1900hrs on normal weekdays)

Location: M2b - Noon-day gun area

			Measur	ement Noi	se Level	Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq	Leq L10		Leq	Leq	Leq
						Unit: dB	(A), (30-min)	
31/8/18	13:40	Cloudy	66.5	66.5 68.4		68	67	75
5/9/18	13:00	Fine	65.6	67.2	63.6	68	66	75
13/9/18	11:25	Cloudy	66.5			68	67	75
21/9/18	15:25	Fine	65.0	65.0 66.6		68	65	75
27/9/18	10:05	Fine	66.5 68.2 64.4		64.4	68	67	75

Location: M3a - Tung Lo Wan Fire Station

			Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq L10 L90		L90	Leq	Leq	Leq
						Unit: dB	(A), (30-min)	
29/8/18	09:50	Fine	65.9	68.0	64.5	69	66	75
4/9/18	10:40	Fine	66.9	69.4	62.3	69	67	75
11/9/18	09:25	Fine	65.9	67.0	64.0	69	66	75
21/9/18	10:05	Fine	67.2 69.6 65.3		69	67	75	
27/9/18	10:40	Fine	64.7 66.2 62.8		69	65	75	



Day Time (0700 - 1900hrs on normal weekdays)

Location: M4b - Victoria Centre

		Measure	ement Noi	se Level		Baseline Noise Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq	Leq L10		Leq	Leq	Leq
						Unit: dB	(A), (30min)	
29/8/18	10:30	Fine	66.0	66.0 69.3		67	66	75
4/9/18	11:17	Fine	66.2	67.7	64.2	67	66	75
11/9/18	08:45	Fine	65.6			67	66	75
21/9/18	10:40	Fine	65.4	65.4 66.8 63		67	65	75
27/9/18	11:00	Fine	66.5 69.8 62.4		62.4	67	67	75

Location: M5b - City Garden

			Measure	ement Noi	se Level	Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq L10 L9		L90	Leq	Leq	Leq
					Unit: dB	(A), (30min)		
31/8/18	08:55	Cloudy	71.0	73.4	68.7	68	68	75
5/9/18	09:23	Fine	71.4	72.5	69.4	68	69	75
11/9/18	11:15	Fine	69.8	71.0	68.3	68	65	75
21/9/18	08:40	Fine	69.5 70.5 68.4		68	64	75	
27/9/18	13:00	Fine	70.4 72.1 68.8		68	67	75	

Location: M6 - HK Baptist Church Henrietta Secondary School

			Measur	ement Noi	se Level	Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq	Leq L10		Leq	Leq	Leq
						Unit: dB((A), (30-min)	
31/8/18	09:35	Cloudy	64.9	64.9 66.1		71	65	70
5/9/18	08:48	Fine	68.1	8.1 69.2 66.8		71	68	70
11/9/18	10:35	Fine	67.0	68.2	65.5	71	67	70
21/9/18	09:15	Fine	66.0	66.0 67.3		71	66	70
27/9/18	13:35	Fine	67.1	67.1 68.2 6		71	67	70



Day Time (0700 - 1900hrs on normal weekdays)

Location: M7e - International Finance Centre (Eastern End of Podium) (Reference Station)

			Measur	ement Noi	se Level	Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq	Leq L10		Leq	Leq	Leq
						Unit: dB((A), (30-min)	
27/8/18	13:45	Fine	67.0	67.0 69.1		67	54	N/A
4/9/18	13:55	Fine	67.4	70.5	63.8	67	59	N/A
11/9/18	15:10	Fine	66.3			67	66	N/A
18/9/18	14:05	Fine	67.4			67	59	N/A
24/9/18	15:30	Fine	65.4	654 675 62		67	65	N/A


Location: M7w - International Finance Centre (Western End of Podium)

			Measure	ement Noi	se Level	Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq L10 L9		L90	Leq	Leq	Leq
						Unit: dB	(A), (30-min)	
27/8/18	13:10	Fine	66.4	68.7	64.0	69	66	75
4/9/18	13:20	Fine	69.3	71.6	64.8	69	69	75
11/9/18	14:30	Fine	64.5	66.1	62.3	69	65	75
18/9/18	13:30	Fine	67.1 69.6 64.4		69	67	75	
24/9/18	14:55	Fine	64.7 65.9 63.1		69	65	75	

Location: M8 - City Hall

			Measurement Noise Lev			Baseline Level	Construction Noise Level	Limit Level
Date	Time	Weather	Leq L10		L90	Leq	Leq	Leq
			200 210 200			Unit: dB	(A), (30-min)	
27/8/18	14:25	Fine	60.4	60.4 62.5 57.7		64	60	70
4/9/18	14:35	Fine	66.9	71.2	57.4	64	64	70
11/9/18	15:54	Fine	59.9	59.9 61.5 57.0		64	60	70
18/9/18	16:52	Fine	60.5 62.8 57.4		57.4	64	61	70
24/9/18	14.05	Fine	59.6 61.7 56.9		64	60	70	




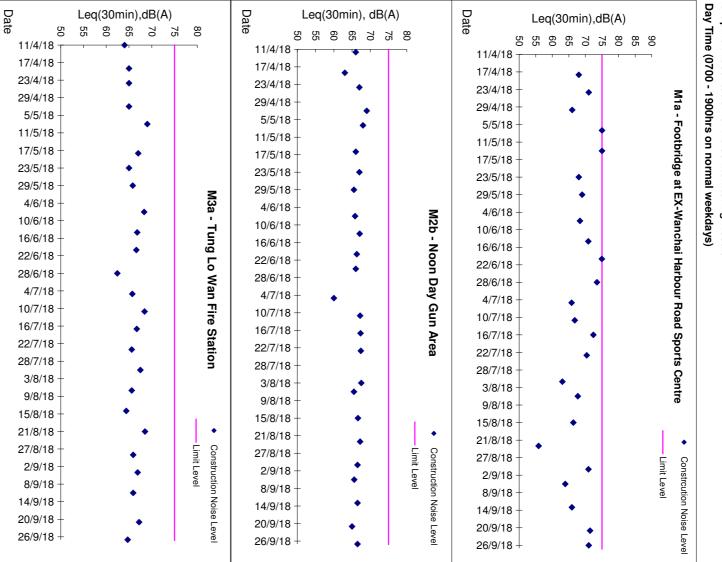

Graphic Presentation of Noise Monitoring Result




Graphic Presentation of Noise Monitoring Result

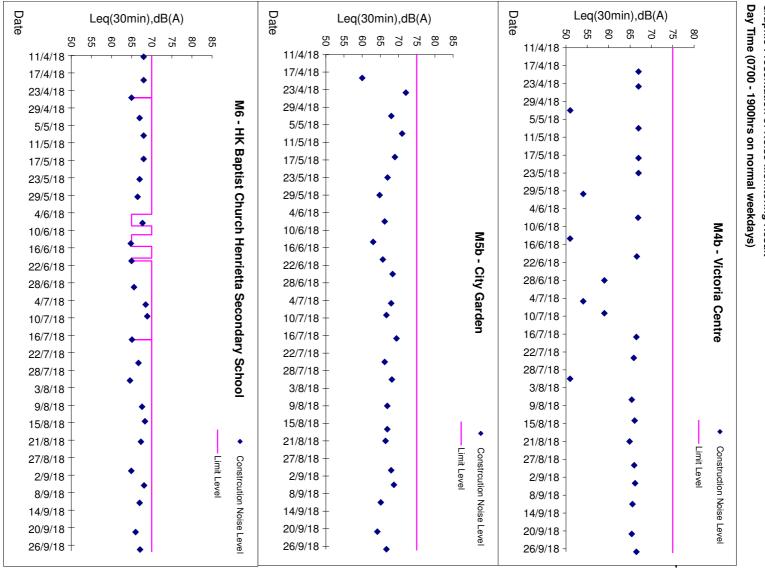



Graphic Presentation of Noise Monitoring Result

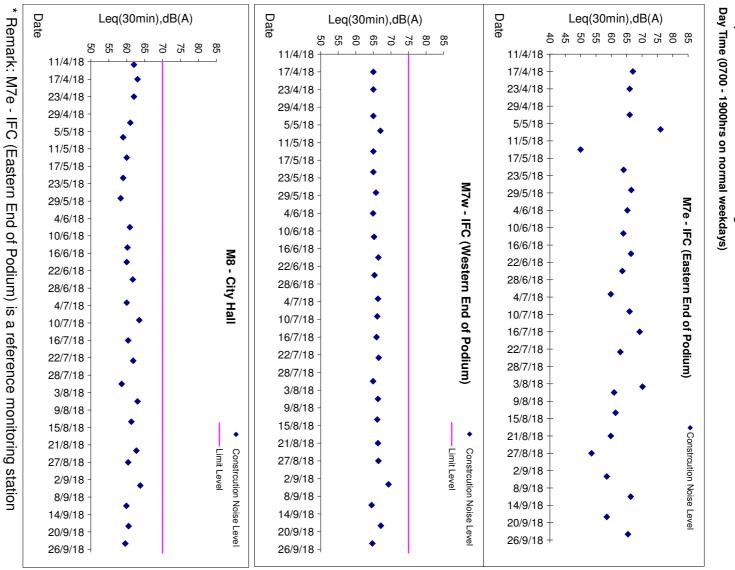



Appendix 5.3 Air Quality Monitoring Results and Graphical Presentations Location: CMA1b - Harbour Grand Hotel Boundary Wall

Report on 24-hour TSP monitoring

Action Level (μg/m3) - 176.7 Limit Level (μg/m3) - 260

Date	Sampling	Weather	Filter paper Filter Weight, g			Elapse Time	Elapse Time, hr		ng Flow Rate, m ³ /min		min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
27-Aug-18	8:00	Rainy	27012	2.6763	2.7284	12324.78	12348.78	24.00	1.19	1.19	1.19	1714	30.4
1-Sep-18	8:00	Cloudy	27245	2.6504	2.6812	12351.78	12375.78	24.00	1.20	1.19	1.19	1718	17.9
7-Sep-18	8:00	Cloudy	27198	2.6884	2.7641	12378.78	12402.78	24.00	1.19	1.19	1.19	1715	44.1
13-Sep-18	8:00	Cloudy	27328	2.6997	2.7555	12405.78	12429.78	24.00	1.19	1.19	1.19	1715	32.5
20-Sep-18	13:00	Cloudy	27437	2.6459	2.7121	12436.89	12460.89	24.00	1.19	1.19	1.19	1715	38.6
24-Sep-18	8:00	Rainy	27440	2.6318	2.6738	12460.89	12484.89	24.00	1.19	1.19	1.19	1719	24.4

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 19 September 2018 to 20 September 2018.

Report on 1-hour TSP monitoring Action Level (µg/m3) - 320.1 Limit Level (µg/m3) - 500

Date	Sampling	Weather	Filter paper	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /ı	min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μ g/m ³
28-Aug-18	8:15	Rainy	26855	2.6679	2.6701	12348.78	12349.78	1.00	1.19	1.19	1.19	71	30.8
28-Aug-18	9:17	Rainy	26799	2.6877	2.6902	12349.78	12350.78	1.00	1.19	1.19	1.19	71	35.0
28-Aug-18	13:00	Rainy	27094	2.6762	2.6823	12350.78	12351.78	1.00	1.19	1.19	1.19	71	85.3
3-Sep-18	9:00	Cloudy	27192	2.6938	2.6955	12375.78	12376.78	1.00	1.19	1.19	1.19	71	23.8
3-Sep-18	10:07	Cloudy	27233	2.6458	2.6488	12376.78	12377.78	1.00	1.19	1.19	1.19	71	42.0
3-Sep-18	13:00	Cloudy	27231	2.6385	2.6415	12377.78	12378.78	1.00	1.19	1.19	1.19	71	42.0
8-Sep-18	8:03	Rainy	27344	2.6719	2.6746	12402.78	12403.78	1.00	1.19	1.19	1.19	72	37.7
8-Sep-18	9:05	Rainy	27341	2.6946	2.7044	12403.78	12404.78	1.00	1.19	1.19	1.19	72	136.9
8-Sep-18	10:08	Rainy	27339	2.6922	2.6996	12404.78	12405.78	1.00	1.19	1.19	1.19	72	103.4
14-Sep-18	9:05	Cloudy	27457	2.6500	2.6527	12429.78	12430.78	1.00	1.19	1.19	1.19	71	37.8
14-Sep-18	10:15	Cloudy	27450	2.6491	2.6523	12430.78	12431.78	1.00	1.19	1.19	1.19	71	44.8
14-Sep-18	14:05	Cloudy	27123	2.6927	2.6951	12431.78	12432.78	1.00	1.19	1.19	1.19	71	33.6
20-Sep-18	8:00	Cloudy	27490	2.6534	2.6568	12433.89	12434.89	1.00	1.19	1.19	1.19	71	47.6
20-Sep-18	9:10	Cloudy	27524	2.6514	2.6560	12434.89	12435.89	1.00	1.19	1.19	1.19	71	64.4
20-Sep-18	10:45	Cloudy	27431	2.6351	2.6388	12435.89	12436.89	1.00	1.19	1.19	1.19	71	51.8
26-Sep-18	9:25	Rainy	27553	2.6555	2.6585	12484.89	12485.89	1.00	1.19	1.19	1.19	72	41.9
26-Sep-18	10:40	Rainy	27583	2.6712	2.6750	12485.89	12486.89	1.00	1.19	1.19	1.19	72	53.1
26-Sep-18	13:00	Rainy	27560	2.6457	2.6494	12486.89	12487.89	1.00	1.30	1.30	1.30	78	47.4

Location: CMA2a - Causeway Bay Community Centre

Report on 24-hour TSP monitoring Action Level (µg/m3) - 169.5 Limit Level (µg/m3) - 260

Date	Sampling	Weather	Filter	Filter Weigh	Filter Weight, g E		ır	Sampling	Flow Rate, m ³ /min			Total	TSP Level,
	Time	Condition	paper no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q_{sf}	Average	Volume, m ³	β μg/m ³
27-Aug-18	8:00	Rainy	27011	2.6676	2.7539	21898.48	21922.48	24.00	1.19	1.19	1.19	1714	50.3
1-Sep-18	8:00	Cloudy	27243	2.6454	2.7125	21925.48	21949.48	24.00	1.20	1.19	1.19	1719	39.0
7-Sep-18	8:00	Cloudy	27197	2.6858	2.8494	21952.48	21976.48	24.00	1.19	1.19	1.19	1715	95.4
13-Sep-18	8:00	Cloudy	27327	2.7071	2.8022	21979.48	22003.48	24.00	1.19	1.19	1.19	1715	55.4
20-Sep-18	11:50	Cloudy	27436	2.6460	2.7461	22010.47	22034.47	24.00	1.19	1.19	1.19	1716	58.3
24-Sep-18	8:00	Rainy	27439	2.6523	2.7260	22034.47	22058.47	24.00	1.20	1.19	1.19	1721	42.8
Remarks: Due to	interruption of e	electricity, the 24	4hr TSP was re	scheduled from	19 September	2018 to 20 Septem	ber 2018.						

Report on 1-hour TSP monitoring Action Level (µg/m3) - 323.4 Limit Level (µg/m3) - 500

Date	Sampling	Weather	Filter	Filter Weigh	nt, g	Elapse Time, h	ır	Sampling	Flo	w Rate, m ³ /r	nin	Total	TSP Level,
	Time	Condition	paper no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
28-Aug-18	8:07	Rainy	26856	2.6759	2.6815	21922.48	21923.48	1.00	1.19	1.19	1.19	71	78.3
28-Aug-18	9:30	Rainy	27088	2.6817	2.6874	21923.48	21924.48	1.00	1.19	1.19	1.19	71	79.7
28-Aug-18	13:00	Rainy	27102	2.6839	2.6940	21924.48	21925.48	1.00	1.19	1.19	1.19	71	141.3
3-Sep-18	8:55	Cloudy	27238	2.6405	2.6439	21949.48	21950.48	1.00	1.19	1.19	1.19	71	47.6
3-Sep-18	10:02	Cloudy	27232	2.6677	2.6732	21950.48	21951.48	1.00	1.19	1.19	1.19	71	77.0
3-Sep-18	13:00	Cloudy	27235	2.6554	2.6604	21951.48	21952.48	1.00	1.19	1.19	1.19	71	70.0
8-Sep-18	8:10	Rainy	27343	2.6920	2.7023	21976.48	21977.48	1.00	1.19	1.19	1.19	72	143.8
8-Sep-18	9:12	Rainy	27342	2.6956	2.7102	21977.48	21978.48	1.00	1.19	1.19	1.19	72	203.8
8-Sep-18	10:15	Rainy	27340	2.6961	2.7087	21978.48	21979.48	1.00	1.19	1.19	1.19	72	175.9
14-Sep-18	8:55	Cloudy	27458	2.6532	2.6600	22003.48	22004.48	1.00	1.19	1.19	1.19	71	95.2
14-Sep-18	10:15	Cloudy	27451	2.6431	2.6513	22004.48	22005.48	1.00	1.19	1.19	1.19	71	114.8
14-Sep-18	14:10	Cloudy	27121	2.6907	2.6954	22005.48	22006.48	1.00	1.19	1.19	1.19	71	65.8
20-Sep-18	8:00	Cloudy	27491	2.6469	2.6532	22007.47	22008.47	1.00	1.19	1.19	1.19	71	88.1
20-Sep-18	9:10	Cloudy	27414	2.6787	2.6902	22008.47	22009.47	1.00	1.19	1.19	1.19	71	160.9
20-Sep-18	10:45	Cloudy	27432	2.6417	2.6513	22009.47	22010.47	1.00	1.19	1.19	1.19	71	134.3
26-Sep-18	9:30	Rainy	27586	2.6526	2.6580	22058.47	22059.47	1.00	1.19	1.19	1.19	72	75.3
26-Sep-18	10:50	Rainy	27580	2.6642	2.6713	22059.47	22060.47	1.00	1.19	1.19	1.19	72	99.1
26-Sep-18	13:00	Rainy	27561	2.6588	2.6669	22060.47	22061.47	1.00	1.19	1.19	1.19	72	113.0

Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring

Action Level (µg/m3) - 171 Limit Level (µg/m3) - 260

Date	Sampling	Weather	Filter	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /	min	Total	TSP Level,
	Time	Condition	paper no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m³
27-Aug-18	8:00	Rainy	27049	2.7030	2.7802	9320.49	9344.49	24.00	1.12	1.13	1.12	1619	47.7
1-Sep-18	8:00	Cloudy	27244	2.6447	2.6798	9347.49	9371.49	24.00	1.07	1.06	1.07	1535	22.9
7-Sep-18	8:00	Cloudy	26447	2.6695	2.7729	9374.49	9398.49	24.00	1.06	1.07	1.06	1531	67.5
13-Sep-18	8:00	Cloudy	27331	2.6828	2.7389	9401.49	9425.49	24.00	1.06	1.06	1.06	1531	36.6
20-Sep-18	11:50	Cloudy	27526	2.6631	2.7385	9438.48	9462.48	24.00	1.06	1.06	1.06	1532	49.2
26-Sep-18	15:15	Rainy	27566	2.6615	2.7694	9474.57	9498.57	24.00	1.13	1.13	1.13	1625	66.4

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 19 and 24 September 2018 to 20 and 26 September 2018 respectively.

Report on 1-hour TSP monitoring Action Level (µg/m3) - 311.3 Limit Level (µg/m3) - 500

Date	Sampling	Weather	Filter	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /	min	Total	TSP Level,
	Time	Condition	paper no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
28-Aug-18	9:45	Rainy	26802	2.6655	2.6699	9344.49	9345.49	1.00	1.13	1.13	1.13	68	65.2
28-Aug-18	13:00	Rainy	27100	2.6892	2.6918	9345.49	9346.49	1.00	1.13	1.13	1.13	68	38.5
28-Aug-18	14:05	Rainy	27097	2.6836	2.6905	9346.49	9347.49	1.00	1.13	1.13	1.13	68	102.2
3-Sep-18	8:45	Cloudy	27240	2.6464	2.6497	9371.49	9372.49	1.00	1.06	1.06	1.06	64	51.7
3-Sep-18	10:00	Cloudy	27028	2.6810	2.6822	9372.49	9373.49	1.00	1.06	1.06	1.06	64	18.8
3-Sep-18	13:00	Cloudy	27220	2.6816	2.6827	9373.49	9374.49	1.00	1.06	1.06	1.06	64	17.2
8-Sep-18	13:00	Rainy	27337	2.6757	2.6802	9398.49	9399.49	1.00	1.07	1.07	1.07	64	70.4
8-Sep-18	14:17	Rainy	27334	2.6844	2.6879	9399.49	9400.49	1.00	1.07	1.07	1.07	64	54.7
8-Sep-18	15:20	Rainy	27333	2.6748	2.6820	9400.49	9401.49	1.00	1.07	1.07	1.07	64	112.6
14-Sep-18	8:45	Cloudy	27400	2.6966	2.6990	9425.49	9426.49	1.00	1.06	1.06	1.06	64	37.7
14-Sep-18	10:05	Cloudy	27452	2.6421	2.6451	9426.49	9427.49	1.00	1.06	1.06	1.06	64	47.1
14-Sep-18	13:00	Cloudy	27403	2.6962	2.6982	9427.49	9428.49	1.00	1.06	1.06	1.06	64	31.4
20-Sep-18	8:00	Cloudy	27410	2.6727	2.6767	9435.48	9436.48	1.00	1.06	1.06	1.06	64	62.7
20-Sep-18	9:15	Cloudy	27590	2.6607	2.6656	9436.48	9437.48	1.00	1.06	1.06	1.06	64	76.8
20-Sep-18	10:47	Cloudy	27430	2.6337	2.6384	9437.48	9438.48	1.00	1.06	1.06	1.06	64	73.7
26-Sep-18	9:05	Rainy	27551	2.6678	2.6717	9471.57	9472.57	1.00	1.19	1.19	1.19	71	54.6
26-Sep-18	10:30	Rainy	27556	2.6508	2.6558	9472.57	9473.57	1.00	1.19	1.19	1.19	71	70.0
26-Sep-18	13:00	Rainy	27577	2.6479	2.6518	9473.57	9474.57	1.00	1.19	1.19	1.19	71	54.6

Location: CMA4a - SPCA

Report on 24-hour TSP monitoring Action Level (µg/m3) - 171.

171.2 Limit Level (µg/m3) -260

Date	Sampling	Weather	Filter	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /i	min	Total	TSP Level,
	Time	Condition	paper no.	Initial	Final	Initial	Final	Time, hr	Initial, Q_{si}	Final, Q _{sf}	Average	Volume, m ³	μ g/m ³
27-Aug-18	8:00	Rainy	27050	2.6878	2.7514	26148.04	26172.04	24.00	1.26	1.26	1.26	1817	35.0
1-Sep-18	8:00	Cloudy	27096	2.7031	2.7552	26175.04	26199.04	24.00	1.27	1.26	1.26	1821	28.6
7-Sep-18	8:00	Cloudy	27195	2.6942	2.7934	26202.04	26226.04	24.00	1.26	1.27	1.26	1818	54.6
13-Sep-18	8:00	Cloudy	27332	2.6859	2.7286	26229.04	26253.04	24.00	1.26	1.26	1.26	1818	23.5
20-Sep-18	11:32	Cloudy	27525	2.6511	2.7204	26266.13	26290.13	24.00	1.26	1.26	1.26	1819	38.1
24-Sep-18	8:00	Rainy	27537	2.6525	2.6984	26290.13	26314.13	24.00	1.27	1.27	1.27	1823	25.2

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 19 September 2018 to 20 September 2018.

Report on 1-hour TSP monitoring

Action Level (μg/m3) -Limit Level (μg/m3) -312.5 500

Date	Sampling	Weather	Filter	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /ı	min	Total	TSP Level,
	Time	Condition	paper no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
28-Aug-18	10:12	Rainy	27234	2.6604	2.6637	26172.04	26173.04	1.00	1.26	1.26	1.26	76	43.5
28-Aug-18	13:00	Rainy	27101	2.6675	2.6805	26173.04	26174.04	1.00	1.26	1.26	1.26	76	171.5
28-Aug-18	14:37	Rainy	27095	2.6938	2.6985	26174.04	26175.04	1.00	1.26	1.26	1.26	76	62.0
3-Sep-18	8:48	Cloudy	27030	2.6619	2.6638	26199.04	26200.04	1.00	1.26	1.26	1.26	76	25.1
3-Sep-18	9:50	Cloudy	27029	2.6770	2.6803	26200.04	26201.04	1.00	1.26	1.26	1.26	76	43.6
3-Sep-18	13:00	Cloudy	27194	2.6822	2.6841	26201.04	26202.04	1.00	1.26	1.26	1.26	76	25.1
8-Sep-18	13:00	Rainy	27338	2.6733	2.6778	26226.04	26227.04	1.00	1.27	1.27	1.27	76	59.3
8-Sep-18	14:03	Rainy	27336	2.6858	2.6884	26227.04	26228.04	1.00	1.27	1.27	1.27	76	34.3
8-Sep-18	15:10	Rainy	27335	2.6891	2.6922	26228.04	26229.04	1.00	1.27	1.27	1.27	76	40.8
14-Sep-18	8:40	Cloudy	27399	2.6991	2.7029	26253.04	26254.04	1.00	1.26	1.26	1.26	76	50.2
14-Sep-18	10:00	Cloudy	27453	2.6556	2.6599	26254.04	26255.04	1.00	1.26	1.26	1.26	76	56.8
14-Sep-18	13:00	Cloudy	27448	2.6484	2.6526	26255.04	26256.04	1.00	1.26	1.26	1.26	76	55.5
20-Sep-18	8:00	Cloudy	27409	2.6693	2.6746	26263.13	26264.13	1.00	1.26	1.26	1.26	76	69.9
20-Sep-18	9:03	Cloudy	27523	2.6563	2.6635	26264.13	26265.13	1.00	1.26	1.26	1.26	76	95.0
20-Sep-18	10:30	Cloudy	27417	2.6908	2.6983	26265.13	26266.13	1.00	1.26	1.26	1.26	76	99.0
26-Sep-18	8:50	Rainy	27550	2.6685	2.6718	26314.13	26315.13	1.00	1.27	1.27	1.27	76	43.5
26-Sep-18	10:25	Rainy	27555	2.6477	2.6532	26315.13	26316.13	1.00	1.27	1.27	1.27	76	72.4
26-Sep-18	13:00	Rainy	27558	2.6639	2.6691	26316.13	26317.13	1.00	1.27	1.27	1.27	76	68.5

Location: CMA5b - Pedestrian Plaza

Report on 24-hour TSP monitoring Action Level (µg/m3) - 181 Limit Level (µg/m3) - 260

Date	Sampling	Weather	Filter paper	Filter Weigh	nt, g	Elapse Time	e, hr	Sampling	Flo	w Rate, m ³ /ı	min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
28-Aug-18	14:30	Rainy	27093	2.6854	2.7166	10744.46	10768.46	24.00	0.90	0.90	0.90	1292	24.1
1-Sep-18	8:00	Cloudy	27176	2.6855	2.7240	10768.46	10792.46	24.00	0.90	0.90	0.90	1296	29.7
7-Sep-18	8:00	Cloudy	27201	2.6739	2.7647	10795.46	10819.46	24.00	0.89	0.90	0.90	1292	70.3
13-Sep-18	8:00	Cloudy	27313	2.6477	2.7116	10822.46	10846.46	24.00	0.90	0.90	0.90	1292	49.4
20-Sep-18	12:30	Cloudy	27527	2.6523	2.7890	10876.49	10900.49	24.00	1.01	1.01	1.01	1461	93.6
24-Sep-18	8:00	Rainy	26912	2.6646	2.7385	10900.49	10924.49	24.00	1.02	1.02	1.02	1465	50.4

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 27 August 2018 and 19 September 2018 to 28 August 2018 and 20 September 2018 respectively.

Report on 1-hour TSP monitoring Action Level (μg/m3) - 332 Limit Level (μg/m3) - 500 332 500

Date	Sampling	Weather	Filter paper	Filter Weigh	nt, g	Elapse Time	ə, hr	Sampling	Flo	w Rate, m ³ /r	min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
28-Aug-18	9:50	Rainy	26750	2.6784	2.6921	10741.46	10742.46	1.00	0.90	0.90	0.90	54	254.3
28-Aug-18	10:53	Rainy	27103	2.6858	2.6891	10742.46	10743.46	1.00	0.90	0.90	0.90	54	61.3
28-Aug-18	13:00	Rainy	27092	2.6716	2.6736	10743.46	10744.46	1.00	0.90	0.90	0.90	54	37.1
3-Sep-18	8:00	Cloudy	27181	2.6523	2.6556	10792.46	10793.46	1.00	0.90	0.90	0.90	54	61.3
3-Sep-18	10:55	Cloudy	27237	2.6313	2.6345	10793.46	10794.46	1.00	0.90	0.90	0.90	54	59.4
3-Sep-18	13:00	Cloudy	27219	2.6750	2.6769	10794.46	10795.46	1.00	0.90	0.90	0.90	54	35.3
8-Sep-18	13:00	Rainy	27295	2.6504	2.6530	10819.46	10820.46	1.00	0.90	0.90	0.90	54	48.2
8-Sep-18	15:24	Rainy	27293	2.6557	2.6594	10820.46	10821.46	1.00	0.90	0.90	0.90	54	68.5
8-Sep-18	16:56	Rainy	27316	2.6403	2.6482	10821.46	10822.46	1.00	0.90	0.90	0.90	54	146.3
14-Sep-18	8:15	Cloudy	27462	2.6501	2.6527	10846.46	10847.46	1.00	0.90	0.90	0.90	54	48.3
14-Sep-18	9:40	Cloudy	27456	2.6400	2.6428	10847.46	10848.46	1.00	0.90	0.90	0.90	54	52.1
14-Sep-18	10:42	Cloudy	27401	2.6959	2.7008	10848.46	10849.46	1.00	0.90	0.90	0.90	54	91.1
20-Sep-18	8:10	Cloudy	27522	2.6308	2.6383	10873.49	10874.49	1.00	0.90	0.90	0.90	54	139.3
20-Sep-18	9:35	Cloudy	27416	2.6998	2.7087	10874.49	10875.49	1.00	0.90	0.90	0.90	54	165.3
20-Sep-18	10:50	Cloudy	27433	2.6334	2.6409	10875.49	10876.49	1.00	0.90	0.90	0.90	54	139.3
26-Sep-18	8:06	Rainy	27548	2.6644	2.6693	10924.49	10925.49	1.00	1.02	1.02	1.02	61	80.3
26-Sep-18	10:00	Rainy	27554	2.6629	2.6702	10925.49	10926.49	1.00	1.02	1.02	1.02	61	119.6
26-Sep-18	15:25	Rainy	27567	2.6582	2.6677	10926.49	10927.49	1.00	1.02	1.02	1.02	61	155.6

Location: MA1e - International Finance Centre (Eastern Wing)

Report on 24-hour TSP monitoring

Action Level (μg/m3) - 173.4 Limit Level (μg/m3) - 260

Date	Sampling	Weather	Filter paper	Filter Weigh	nt, g	Elapse Time	e, hr	Sampling	Flo	w Rate, m ³ /ı	min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
28-Aug-18	11:15	Rainy	27033	2.6771	2.7389	23044.53	23068.53	24.00	1.17	1.17	1.17	1683	36.7
3-Sep-18	15:17	Cloudy	27184	2.6772	2.7186	23095.52	23119.52	24.00	1.12	1.12	1.12	1616	25.6
7-Sep-18	8:00	Cloudy	27205	2.6537	2.7397	23119.52	23143.52	24.00	1.12	1.22	1.17	1684	51.1
13-Sep-18	8:00	Cloudy	27289	2.6513	2.6996	23146.52	23170.52	24.00	1.17	1.17	1.17	1684	28.7
20-Sep-18	16:15	Cloudy	27528	2.6401	2.6981	23176.52	23200.52	24.00	1.12	1.12	1.12	1618	35.8
24-Sep-18	8:00	Rainy	27545	2.6577	2.6960	23200.52	23224.52	24.00	1.13	1.13	1.13	1621	23.6

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 27 August 2018, 1 and 19 September 2018 to 28 August 2018, 3 and 20 September 2018 respectively.

Report on 1-hour TSP monitoring

 Action Level (μg/m3) 325.1

 Limit Level (μg/m3) 500

			Filter paper							2			
Date	Sampling	Weather	no.	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /i	min	Total	TSP Level
	Time	Condition		Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
28-Aug-18	8:00	Rainy	27053	2.6848	2.7021	23041.53	23042.53	1.00	1.12	1.12	1.12	67	256.6
28-Aug-18	9:03	Rainy	27047	2.6832	2.6865	23042.53	23043.53	1.00	1.17	1.17	1.17	70	47.0
28-Aug-18	10:10	Rainy	27044	2.6637	2.6700	23043.53	23044.53	1.00	1.17	1.17	1.17	70	89.8
3-Sep-18	10:09	Cloudy	27190	2.6626	2.6690	23092.52	23093.52	1.00	1.12	1.12	1.12	67	95.0
3-Sep-18	13:00	Cloudy	27186	2.6632	2.6659	23093.52	23094.52	1.00	1.12	1.12	1.12	67	40.1
3-Sep-18	14:02	Cloudy	27185	2.6809	2.6825	23094.52	23095.52	1.00	1.12	1.12	1.12	67	23.7
8-Sep-18	9:35	Rainy	27326	2.7005	2.7047	23143.52	23144.52	1.00	1.17	1.22	1.19	72	58.6
8-Sep-18	10:42	Rainy	27323	2.6974	2.7007	23144.52	23145.52	1.00	1.13	1.17	1.15	69	47.9
8-Sep-18	13:00	Rainy	27321	2.6949	2.6987	23145.52	23146.52	1.00	1.13	1.13	1.13	68	56.3
14-Sep-18	8:45	Cloudy	27286	2.6533	2.6559	23170.52	23171.52	1.00	1.12	1.12	1.12	67	38.6
14-Sep-18	9:55	Cloudy	27310	2.6574	2.6605	23171.52	23172.52	1.00	1.21	1.21	1.21	73	42.5
14-Sep-18	11:00	Cloudy	26908	2.6637	2.6673	23172.52	23173.52	1.00	1.17	1.17	1.17	70	51.3
20-Sep-18	09:18	Cloudy	26900	2.6753	2.6800	23173.52	23174.52	1.00	1.12	1.12	1.12	67	69.7
20-Sep-18	13:00	Cloudy	27213	2.6768	2.6843	23174.52	23175.52	1.00	1.12	1.12	1.12	67	111.3
20-Sep-18	15:05	Cloudy	27531	2.6485	2.6521	23175.52	23176.52	1.00	1.12	1.12	1.12	67	53.4
26-Sep-18	9:14	Rainy	27024	2.6863	2.6886	23224.52	23225.52	1.00	1.13	1.13	1.13	68	34.1
26-Sep-18	10:25	Rainy	27427	2.6583	2.6616	23225.52	23226.52	1.00	1.22	1.22	1.22	73	45.2
26-Sep-18	13:00	Rainy	27424	2.6371	2.6423	23226.52	23227.52	1.00	1.22	1.22	1.22	73	71.2

Location: MA1w - International Finance Centre (Western Wing)

Report on 24-hour TSP monitoring

Action Level (μg/m3) - 173.4 Limit Level (μg/m3) - 260

Date	Sampling	Weather	Filter paper	Filter Weigh	nt, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /ı	min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
27-Aug-18	8:00	Rainy	27054	2.6781	2.7735	22812.86	22836.86	24.00	1.43	1.43	1.43	2062	46.3
1-Sep-18	8:00	Cloudy	27031	2.6625	2.7447	22839.86	22863.86	24.00	1.44	1.43	1.43	2066	39.8
7-Sep-18	8:00	Cloudy	27187	2.6786	2.8052	22866.86	22890.86	24.00	1.37	1.38	1.38	1982	63.9
13-Sep-18	8:00	Cloudy	27315	2.6543	2.7208	22893.86	22917.86	24.00	1.43	1.43	1.43	2063	32.2
20-Sep-18	16:10	Cloudy	27530	2.6482	2.7913	22947.94	22971.94	24.00	1.43	1.43	1.43	2063	69.3
24-Sep-18	8:00	Rainy	27546	2.6873	2.7588	22971.94	22995.94	24.00	1.44	1.44	1.44	2068	34.6

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 19 September 2018 to 20 September 2018.

Report on 1-hour TSP monitoring


Action Level (µg/m3) - 325.1

Limit Level (µg/m3) - 500


Date	Sampling	Weather	Filter paper	Filter Weigh	it, g	Elapse Tim	e, hr	Sampling	Flo	w Rate, m ³ /r	min	Total	TSP Level,
	Time	Condition	no.	Initial	Final	Initial	Final	Time, hr	Initial, Q _{si}	Final, Q _{sf}	Average	Volume, m ³	μg/m ³
28-Aug-18	8:03	Rainy	27048	2.6954	2.6984	22836.86	22837.86	1.00	1.32	1.32	1.32	79	37.8
28-Aug-18	9:06	Rainy	27045	2.6792	2.6880	22837.86	22838.86	1.00	1.32	1.32	1.32	79	111.0
28-Aug-18	10:12	Rainy	27034	2.6692	2.6748	22838.86	22839.86	1.00	1.38	1.38	1.38	83	67.8
3-Sep-18	8:33	Cloudy	27191	2.6605	2.6650	22863.86	22864.86	1.00	1.43	1.43	1.43	86	52.4
3-Sep-18	9:45	Cloudy	27189	2.6634	2.6683	22864.86	22865.86	1.00	1.38	1.38	1.38	83	59.3
3-Sep-18	10:56	Cloudy	27188	2.6727	2.6783	22865.86	22866.86	1.00	1.38	1.38	1.38	83	67.8
8-Sep-18	9:32	Rainy	27182	2.6640	2.6688	22890.86	22891.86	1.00	1.38	1.38	1.38	83	58.0
8-Sep-18	10:36	Rainy	27324	2.6983	2.7039	22891.86	22892.86	1.00	1.38	1.38	1.38	83	67.7
8-Sep-18	13:00	Rainy	27322	2.7038	2.7149	22892.86	22893.86	1.00	1.38	1.38	1.38	83	134.1
14-Sep-18	8:40	Cloudy	27287	2.6491	2.6533	22917.86	22918.86	1.00	1.38	1.38	1.38	83	50.9
14-Sep-18	9:52	Cloudy	27311	2.6548	2.6595	22918.86	22919.86	1.00	1.43	1.43	1.43	86	54.7
14-Sep-18	10:57	Cloudy	26909	2.6638	2.6678	22919.86	22920.86	1.00	1.43	1.43	1.43	86	46.6
20-Sep-18	9:15	Cloudy	26901	2.6837	2.6910	22944.94	22945.94	1.00	1.43	1.43	1.43	86	84.9
20-Sep-18	13:00	Cloudy	27214	2.6693	2.6796	22945.94	22946.94	1.00	1.43	1.43	1.43	86	119.8
20-Sep-18	15:00	Cloudy	27532	2.6512	2.6620	22946.94	22947.94	1.00	1.43	1.43	1.43	86	125.6
26-Sep-18	9:05	Rainy	27587	2.6445	2.6517	22995.94	22996.94	1.00	1.44	1.44	1.44	86	83.6
26-Sep-18	10:18	Rainy	27428	2.6457	2.6518	22996.94	22997.94	1.00	1.44	1.44	1.44	86	70.8
26-Sep-18	13:00	Rainy	27425	2.6404	2.6509	22997.94	22998.94	1.00	1.44	1.44	1.44	86	121.9



Graphic Presentation of 1 hour TSP Result

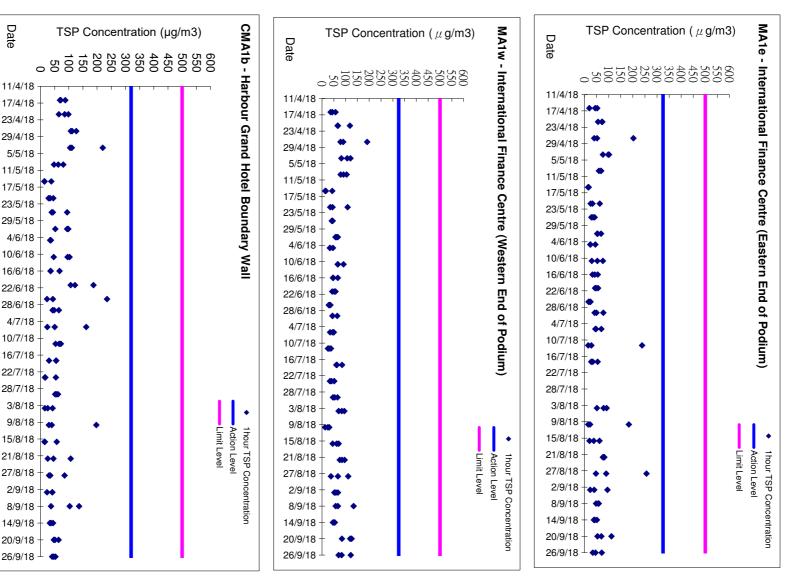




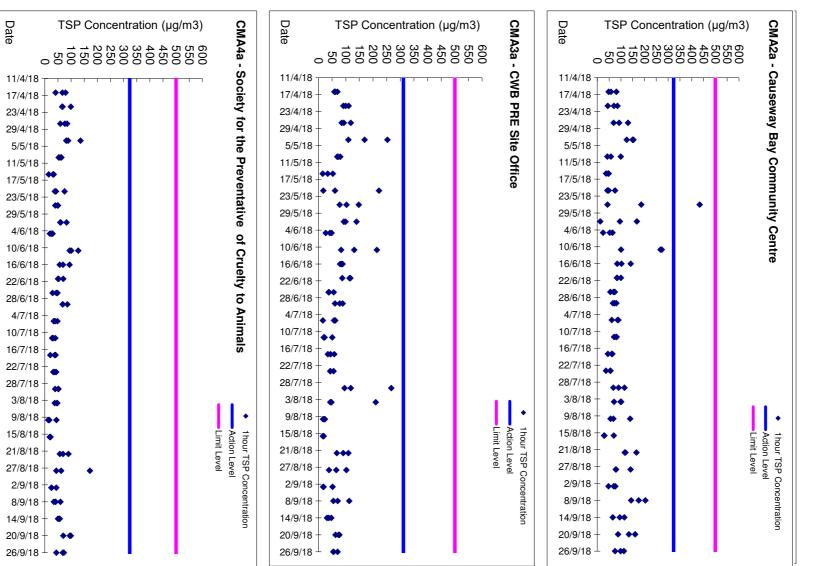

Graphic Presentation of 1 hour TSP Result





Graphic Presentation of 1 hour TSP Result

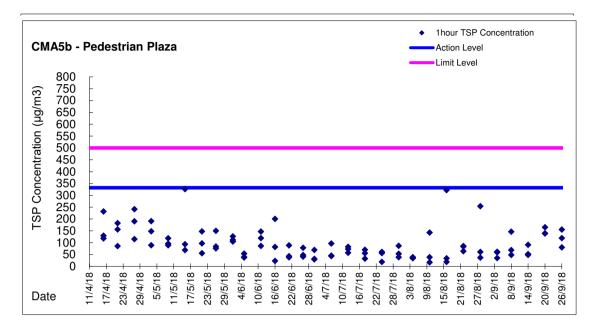



Graphic Presentation of 24 hour TSP Result

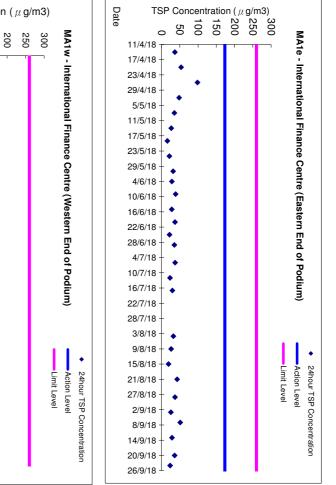


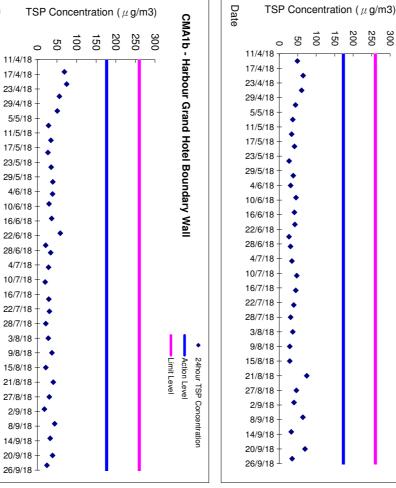

Date



Contract no. HK/2015/01 Wanchai Development Phase II and Central Wanchai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

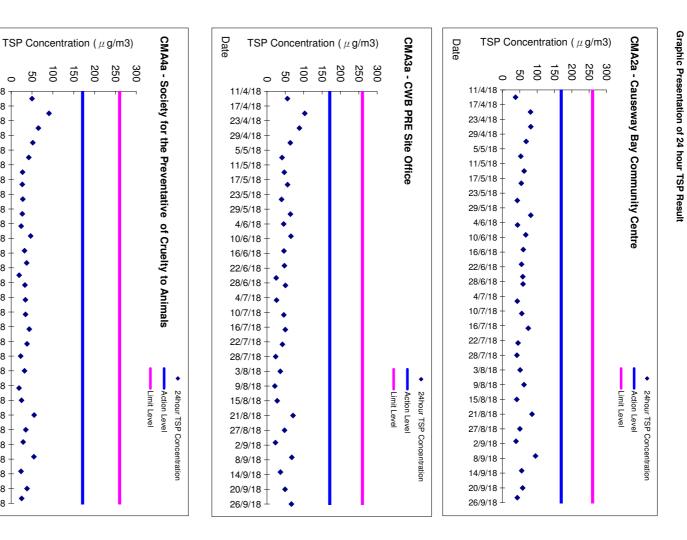

Date

0

٠

٠

٠

٠

٠

٠

٠

٠

٠

٠

٠

٠

٠

•

٠

٠

٠

•

٠

٠

11/4/18

17/4/18

23/4/18

29/4/18

5/5/18

11/5/18

17/5/18

23/5/18

29/5/18

4/6/18

10/6/18 -

16/6/18

22/6/18

28/6/18 -

4/7/18

10/7/18 -

16/7/18 -

22/7/18

28/7/18 +

3/8/18 +

9/8/18 +

15/8/18 + •

21/8/18

27/8/18 -

2/9/18 +

8/9/18


14/9/18 -

20/9/18 -

26/9/18 1



Graphic Presentation of 24 hour TSP Result





Appendix 5.4 Real Time Noise Monitoring Results and Graphical Presentations

Deal time Naisa	Data	DTN1 (Food and F	n in an antal I	lucione Department	Denet)					
Real-time Noise Normal Day 07:		31/8/18 12:31	69	Hygiene Department 6/9/18 7:01	Depot) 68	11/9/18 13:31	69	17/9/18 8:01	70	21/9/18 14:31 69
27/8/18 7:01	68	31/8/18 13:01 31/8/18 13:31	69 69	6/9/18 7:31 6/9/18 8:01	70 69	11/9/18 14:01 11/9/18 14:31	69 69	17/9/18 8:31 17/9/18 9:01	70 70	21/9/18 15:01 69 21/9/18 15:31 69
27/8/18 7:31	70	31/8/18 14:01	69	6/9/18 8:31	69	11/9/18 15:01	69	17/9/18 9:31	70	21/9/18 16:01 69
27/8/18 8:01	70	31/8/18 14:31	68	6/9/18 9:01	70	11/9/18 15:31	68	17/9/18 10:01	69 70	21/9/18 16:31 69
27/8/18 8:31 27/8/18 9:01	69 69	31/8/18 15:01 31/8/18 15:31	69 69	6/9/18 9:31 6/9/18 10:01	70 69	11/9/18 16:01 11/9/18 16:31	68 68	17/9/18 10:31 17/9/18 11:01	70 70	21/9/18 17:01 68 21/9/18 17:31 68
27/8/18 9:31	70	31/8/18 16:01	69	6/9/18 10:31	70	11/9/18 17:01	69	17/9/18 11:31	70	21/9/18 18:01 68
27/8/18 10:01 27/8/18 10:31	70 71	31/8/18 16:31 31/8/18 17:01	69 69	6/9/18 11:01 6/9/18 11:31	70 70	11/9/18 17:31 11/9/18 18:01	69 68	17/9/18 12:01 17/9/18 12:31	70 66	21/9/18 18:31 68 22/9/18 7:01 68
27/8/18 11:01	69	31/8/18 17:31	69	6/9/18 12:01	70	11/9/18 18:31	68	17/9/18 13:01	69	22/9/18 7:31 69
27/8/18 11:31 27/8/18 12:01	68 69	31/8/18 18:01 31/8/18 18:31	69 69	6/9/18 12:31 6/9/18 13:01	70 70	12/9/18 7:01 12/9/18 7:31	68 69	17/9/18 13:31 17/9/18 14:01	70 70	22/9/18 8:01 70 22/9/18 8:31 70
27/8/18 12:31	70	1/9/18 7:01	68	6/9/18 13:31	70	12/9/18 8:01	69	17/9/18 14:31	70	22/9/18 9:01 70
27/8/18 13:01	70 70	1/9/18 7:31	69 70	6/9/18 14:01	70	12/9/18 8:31	69	17/9/18 15:01	70 70	22/9/18 9:31 70
27/8/18 13:31 27/8/18 14:01	70 70	1/9/18 8:01 1/9/18 8:31	70 70	6/9/18 14:31 6/9/18 15:01	69 69	12/9/18 9:01 12/9/18 9:31	69 71	17/9/18 15:31 17/9/18 16:01	70 70	22/9/18 10:01 70 22/9/18 10:31 70
27/8/18 14:31	70	1/9/18 9:01	71	6/9/18 15:31	70	12/9/18 10:01	69	17/9/18 16:31	70	22/9/18 11:01 70
27/8/18 15:01 27/8/18 15:31	70 70	1/9/18 9:31 1/9/18 10:01	70 70	6/9/18 16:01 6/9/18 16:31	69 70	12/9/18 10:31 12/9/18 11:01	69 69	17/9/18 17:01 17/9/18 17:31	70 70	22/9/18 11:31 69 22/9/18 12:01 69
27/8/18 16:01	70	1/9/18 10:31	70	6/9/18 17:01	70	12/9/18 11:31	69	17/9/18 18:01	70	22/9/18 12:31 69
27/8/18 16:31 27/8/18 17:01	70 70	1/9/18 11:01 1/9/18 11:31	70 71	6/9/18 17:31 6/9/18 18:01	70 69	12/9/18 12:01 12/9/18 12:31	69 69	17/9/18 18:31 18/9/18 7:01	70 70	22/9/18 13:01 69 22/9/18 13:31 69
27/8/18 17:31	70	1/9/18 12:01	70	6/9/18 18:31	69	12/9/18 13:01	69	18/9/18 7:31	70	22/9/18 14:01 69
27/8/18 18:01 27/8/18 18:31	70 69	1/9/18 12:31 1/9/18 13:01	70 71	7/9/18 7:01 7/9/18 7:31	68 70	12/9/18 13:31 12/9/18 14:01	69 69	18/9/18 8:01 18/9/18 8:31	70 68	22/9/18 14:31 69 22/9/18 15:01 69
28/8/18 7:01	68	1/9/18 13:31	72	7/9/18 8:01	69	12/9/18 14:31	69	18/9/18 9:01	69	22/9/18 15:31 69
28/8/18 7:31 28/8/18 8:01	69 68	1/9/18 14:01 1/9/18 14:31	70 70	7/9/18 8:31 7/9/18 9:01	69 69	12/9/18 15:01 12/9/18 15:31	69 70	18/9/18 9:31 18/9/18 10:01	70 71	22/9/18 16:01 69 22/9/18 16:31 69
28/8/18 8:31	68	1/9/18 15:01	70	7/9/18 9:31	70	12/9/18 16:01	69	18/9/18 10:31	71	22/9/18 17:01 70
28/8/18 9:01 28/8/18 9:31	68 69	1/9/18 15:31 1/9/18 16:01	69 69	7/9/18 10:01 7/9/18 10:31	70 70	12/9/18 16:31 12/9/18 17:01	69 69	18/9/18 11:01 18/9/18 11:31	70 71	22/9/18 17:31 70 22/9/18 18:01 69
28/8/18 10:01	68	1/9/18 16:31	70	7/9/18 11:01	69	12/9/18 17:31	69	18/9/18 12:01	70	22/9/18 18:31 68
28/8/18 10:31	69	1/9/18 17:01	70	7/9/18 11:31	69	12/9/18 18:01	69	18/9/18 12:31	70	24/9/18 7:01 68
28/8/18 11:01 28/8/18 11:31	69 69	1/9/18 17:31 1/9/18 18:01	70 69	7/9/18 12:01 7/9/18 12:31	69 70	12/9/18 18:31 13/9/18 7:01	69 68	18/9/18 13:01 18/9/18 13:31	70 71	24/9/18 7:31 70 24/9/18 8:01 70
28/8/18 12:01	68	1/9/18 18:31	69	7/9/18 13:01	70	13/9/18 7:31	69	18/9/18 14:01	70	24/9/18 8:31 69
28/8/18 12:31 28/8/18 13:01	70 72	3/9/18 7:01 3/9/18 7:31	68 69	7/9/18 13:31 7/9/18 14:01	70 69	13/9/18 8:01 13/9/18 8:31	69 69	18/9/18 14:31 18/9/18 15:01	70 70	24/9/18 9:01 70 24/9/18 9:31 55
28/8/18 13:31	73	3/9/18 8:01	69	7/9/18 14:31	70	13/9/18 9:01	69	18/9/18 15:31	70	24/9/18 10:01 65
28/8/18 14:01 28/8/18 14:31	71 70	3/9/18 8:31 3/9/18 9:01	69 70	7/9/18 15:01 7/9/18 15:31	69 69	13/9/18 9:31 13/9/18 10:01	69 70	18/9/18 16:01 18/9/18 16:31	70 70	24/9/18 10:31 72 24/9/18 11:01 70
28/8/18 15:01	70	3/9/18 9:31	69	7/9/18 16:01	70	13/9/18 10:31	70	18/9/18 17:01	70	24/9/18 11:31 70
28/8/18 15:31 28/8/18 16:01	70 69	3/9/18 10:01 3/9/18 10:31	70 70	7/9/18 16:31 7/9/18 17:01	70 69	13/9/18 11:01 13/9/18 11:31	70 70	18/9/18 17:31 18/9/18 18:01	70 69	24/9/18 12:01 69 24/9/18 12:31 68
28/8/18 16:31	69	3/9/18 11:01	70	7/9/18 17:31	69	13/9/18 12:01	70	18/9/18 18:31	68	24/9/18 12:31 68
28/8/18 17:01	69	3/9/18 11:31	70	7/9/18 18:01	69	13/9/18 12:31	70	19/9/18 7:01	68	24/9/18 13:31 69
28/8/18 17:31 28/8/18 18:01	70 70	3/9/18 12:01 3/9/18 12:31	69 70	7/9/18 18:31 8/9/18 7:01	68 68	13/9/18 13:01 13/9/18 13:31	70 70	19/9/18 7:31 19/9/18 8:01	70 70	24/9/18 14:01 70 24/9/18 14:31 70
28/8/18 18:31	68	3/9/18 13:01	70	8/9/18 7:31	69	13/9/18 14:01	70	19/9/18 8:31	69	24/9/18 15:01 70
29/8/18 7:01 29/8/18 7:31	68 69	3/9/18 13:31 3/9/18 14:01	70 70	8/9/18 8:01 8/9/18 8:31	70 69	13/9/18 14:31 13/9/18 15:01	70 69	19/9/18 9:01 19/9/18 9:31	69 70	24/9/18 15:31 70 24/9/18 16:01 70
29/8/18 8:01	69	3/9/18 14:31	70	8/9/18 9:01	70	13/9/18 15:31	69	19/9/18 10:01	70	24/9/18 16:31 70
29/8/18 8:31 29/8/18 9:01	69 69	3/9/18 15:01 3/9/18 15:31	70 70	8/9/18 9:31 8/9/18 10:01	70 70	13/9/18 16:01 13/9/18 16:31	69 70	19/9/18 10:31 19/9/18 11:01	71 70	24/9/18 17:01 69 24/9/18 17:31 69
29/8/18 9:31	69	3/9/18 16:01	70	8/9/18 10:31	70	13/9/18 17:01	70	19/9/18 11:31	69	24/9/18 18:01 69
29/8/18 10:01	69 70	3/9/18 16:31	70 70	8/9/18 11:01	70 69	13/9/18 17:31 13/9/18 18:01	69 68	19/9/18 12:01	68 68	24/9/18 18:31 68 26/9/18 7:01 69
29/8/18 10:31 29/8/18 11:01	70	3/9/18 17:01 3/9/18 17:31	70	8/9/18 11:31 8/9/18 12:01	69	13/9/18 18:31	69	19/9/18 12:31 19/9/18 13:01	69	26/9/18 7:01 69 26/9/18 7:31 70
29/8/18 11:31	69 69	3/9/18 18:01	70	8/9/18 12:31	69 71	14/9/18 7:01	68	19/9/18 13:31	70	26/9/18 8:01 70
29/8/18 12:01 29/8/18 12:31	69 71	3/9/18 18:31 4/9/18 7:01	70 68	8/9/18 13:01 8/9/18 13:31	71 68	14/9/18 7:31 14/9/18 8:01	70 69	19/9/18 14:01 19/9/18 14:31	70 69	26/9/18 8:31 69 26/9/18 9:01 70
29/8/18 13:01	70	4/9/18 7:31	70	8/9/18 14:01	71	14/9/18 8:31	69	19/9/18 15:01	70	26/9/18 9:31 69
29/8/18 13:31 29/8/18 14:01	70 68	4/9/18 8:01 4/9/18 8:31	70 69	8/9/18 14:31 8/9/18 15:01	70 69	14/9/18 9:01 14/9/18 9:31	69 70	19/9/18 15:31 19/9/18 16:01	70 69	26/9/18 10:01 69 26/9/18 10:31 68
29/8/18 14:31	68	4/9/18 9:01	69	8/9/18 15:31	70	14/9/18 10:01	70	19/9/18 16:31	69	26/9/18 11:01 69
29/8/18 15:01 29/8/18 15:31	68 68	4/9/18 9:31 4/9/18 10:01	70 70	8/9/18 16:01 8/9/18 16:31	70 70	14/9/18 10:31 14/9/18 11:01	69 70	19/9/18 17:01 19/9/18 17:31	70 69	26/9/18 11:31 70 26/9/18 12:01 70
29/8/18 16:01	69	4/9/18 10:31	70	8/9/18 17:01	70	14/9/18 11:31	70	19/9/18 18:01	69	26/9/18 12:31 70
29/8/18 16:31 29/8/18 17:01	69 70	4/9/18 11:01 4/9/18 11:31	69 70	8/9/18 17:31 8/9/18 18:01	70 70	14/9/18 12:01 14/9/18 12:31	69 69	19/9/18 18:31 20/9/18 7:01	68 68	26/9/18 13:01 69 26/9/18 13:31 70
29/8/18 17:31	70	4/9/18 12:01	70	8/9/18 18:31	69	14/9/18 13:01	70	20/9/18 7:31	70	26/9/18 14:01 70
29/8/18 18:01 29/8/18 18:31	69 69	4/9/18 12:31 4/9/18 13:01	70 70	10/9/18 7:01 10/9/18 7:31	69 70	14/9/18 13:31 14/9/18 14:01	70 70	20/9/18 8:01 20/9/18 8:31	70 69	26/9/18 14:31 70 26/9/18 15:01 70
30/8/18 7:01	68	4/9/18 13:31	70	10/9/18 8:01	69	14/9/18 14:31	70	20/9/18 9:01	69	26/9/18 15:31 70
30/8/18 7:31	69 60	4/9/18 14:01	70	10/9/18 8:31 10/9/18 9:01	69 60	14/9/18 15:01	70	20/9/18 9:31 20/9/18 10:01	70 70	26/9/18 16:01 69 26/9/18 16:31 70
30/8/18 8:01 30/8/18 8:31	69 68	4/9/18 14:31 4/9/18 15:01	70 70	10/9/18 9:31	69 70	14/9/18 15:31 14/9/18 16:01	69 70	20/9/18 10:01	70 70	26/9/18 16:31 70 26/9/18 17:01 70
30/8/18 9:01	68	4/9/18 15:31	70	10/9/18 10:01	71	14/9/18 16:31 14/9/18 17:01	70	20/9/18 11:01	70	26/9/18 17:31 69
30/8/18 9:31 30/8/18 10:01	68 69	4/9/18 16:01 4/9/18 16:31	69 70	10/9/18 10:31 10/9/18 11:01	71 71	14/9/18 17:01	70 70	20/9/18 11:31 20/9/18 12:01	70 69	26/9/18 18:01 69 26/9/18 18:31 69
30/8/18 10:31	70	4/9/18 17:01	70	10/9/18 11:31	70	14/9/18 18:01	69	20/9/18 12:31	68	Newsel Dev 10:00 00:00
30/8/18 11:01 30/8/18 11:31	70 68	4/9/18 17:31 4/9/18 18:01	70 69	10/9/18 12:01 10/9/18 12:31	69 69	14/9/18 18:31 15/9/18 7:01	69 69	20/9/18 13:01 20/9/18 13:31	69 70	Normal Day 19:00-23:00, Sunday & Holiday
30/8/18 12:01	68	4/9/18 18:31	69	10/9/18 13:01	70	15/9/18 7:31	69	20/9/18 14:01	69	07:00-23:00
30/8/18 12:31 30/8/18 13:01	70 70	5/9/18 7:01 5/9/18 7:31	68 70	10/9/18 13:31 10/9/18 14:01	70 70	15/9/18 8:01 15/9/18 8:31	70 69	20/9/18 14:31 20/9/18 15:01	69 69	27/8/18 19:01 69
30/8/18 13:31	70	5/9/18 8:01	70	10/9/18 14:31	70	15/9/18 9:01	70	20/9/18 15:31	69	27/8/18 19:06 69
30/8/18 14:01	70 69	5/9/18 8:31	69 70	10/9/18 15:01	69 69	15/9/18 9:31	70	20/9/18 16:01	69 69	27/8/18 19:11 69 27/8/18 19:16 60
30/8/18 14:31 30/8/18 15:01	69 69	5/9/18 9:01 5/9/18 9:31	70 70	10/9/18 15:31 10/9/18 16:01	69 70	15/9/18 10:01 15/9/18 10:31	69 70	20/9/18 16:31 20/9/18 17:01	69 68	27/8/18 19:16 60 27/8/18 19:21 69
30/8/18 15:31	69 69	5/9/18 10:01	70 70	10/9/18 16:31	70 70	15/9/18 11:01	70 69	20/9/18 17:31	68 68	27/8/18 19:26 49
30/8/18 16:01 30/8/18 16:31	69 70	5/9/18 10:31 5/9/18 11:01	70 70	10/9/18 17:01 10/9/18 17:31	70 70	15/9/18 11:31 15/9/18 12:01	69 69	20/9/18 18:01 20/9/18 18:31	68 68	27/8/18 19:31 69 27/8/18 19:36 69
30/8/18 17:01	70	5/9/18 11:31	70	10/9/18 18:01	70	15/9/18 12:31	69	21/9/18 7:01	68	27/8/18 19:41 69
30/8/18 17:31 30/8/18 18:01	69 69	5/9/18 12:01 5/9/18 12:31	70 70	10/9/18 18:31 11/9/18 7:01	69 68	15/9/18 13:01 15/9/18 13:31	69 69	21/9/18 7:31 21/9/18 8:01	69 69	27/8/18 19:46 69 27/8/18 19:51 69
30/8/18 18:31	70	5/9/18 13:01	70	11/9/18 7:31	69	15/9/18 14:01	70	21/9/18 8:31	69	27/8/18 19:56 68
31/8/18 7:01 31/8/18 7:31	68 69	5/9/18 13:31 5/9/18 14:01	70 70	11/9/18 8:01 11/9/18 8:31	69 69	15/9/18 14:31 15/9/18 15:01	69 69	21/9/18 9:01 21/9/18 9:31	69 69	27/8/18 20:01 68 27/8/18 20:06 68
31/8/18 8:01	70	5/9/18 14:31	69	11/9/18 9:01	70	15/9/18 15:31	69	21/9/18 10:01	70	27/8/18 20:11 68
31/8/18 8:31 31/8/18 9:01	69 68	5/9/18 15:01 5/9/18 15:31	69 69	11/9/18 9:31 11/9/18 10:01	70 70	15/9/18 16:01 15/9/18 16:31	69 69	21/9/18 10:31 21/9/18 11:01	70 70	27/8/18 20:16 68 27/8/18 20:21 68
31/8/18 9:31	68	5/9/18 16:01	69 69	11/9/18 10:31	70	15/9/18 17:01	70	21/9/18 11:31	70	27/8/18 20:26 68
31/8/18 10:01	69	5/9/18 16:31	69 70	11/9/18 11:01	70	15/9/18 17:31	70	21/9/18 12:01	70	27/8/18 20:31 69
31/8/18 10:31 31/8/18 11:01	70 69	5/9/18 17:01 5/9/18 17:31	70 70	11/9/18 11:31 11/9/18 12:01	68 68	15/9/18 18:01 15/9/18 18:31	69 69	21/9/18 12:31 21/9/18 13:01	69 70	27/8/18 20:36 54 27/8/18 20:41 69
31/8/18 11:31	69	5/9/18 18:01	69	11/9/18 12:31	68	17/9/18 7:01	68	21/9/18 13:31	69	27/8/18 20:46 68
31/8/18 12:01	69	5/9/18 18:31	69	11/9/18 13:01	69	17/9/18 7:31	69	21/9/18 14:01	69	27/8/18 20:51 68

Real-time Noise Data 27/8/18 20:56 54	RTN1 (Food and Environmental F 29/8/18 22:01 68	1/9/18 19:06 68	2/9/18 12:11 68	2/9/18 21:16 68	4/9/18 22:21 67
27/8/18 21:01 54 27/8/18 21:06 69	29/8/18 22:06 67 29/8/18 22:11 68	1/9/18 19:11 68 1/9/18 19:16 68	2/9/18 12:16 69 2/9/18 12:21 68	2/9/18 21:21 68 2/9/18 21:26 68	4/9/18 22:26 67 4/9/18 22:31 67
27/8/18 21:11 69	29/8/18 22:16 68	1/9/18 19:21 69	2/9/18 12:26 68	2/9/18 21:31 68	4/9/18 22:36 68
27/8/18 21:16 57	29/8/18 22:21 68	1/9/18 19:26 69	2/9/18 12:31 66	2/9/18 21:36 60	4/9/18 22:41 67
27/8/18 21:21 56 27/8/18 21:26 69	29/8/18 22:26 68 29/8/18 22:31 68	1/9/18 19:31 69 1/9/18 19:36 69	2/9/18 12:36 65 2/9/18 12:41 65	2/9/18 21:41 62 2/9/18 21:46 68	4/9/18 22:46 67 4/9/18 22:51 67
27/8/18 21:31 69	29/8/18 22:36 68	1/9/18 19:41 69	2/9/18 12:46 65	2/9/18 21:51 67	4/9/18 22:56 67
27/8/18 21:36 69	29/8/18 22:41 68	1/9/18 19:46 69	2/9/18 12:51 63	2/9/18 21:56 68	5/9/18 19:01 69
27/8/18 21:41 69 27/8/18 21:46 69	29/8/18 22:46 67 29/8/18 22:51 69	1/9/18 19:51 69 1/9/18 19:56 69	2/9/18 12:56 64 2/9/18 13:01 65	2/9/18 22:01 68 2/9/18 22:06 68	5/9/18 19:06 69 5/9/18 19:11 69
27/8/18 21:51 69	29/8/18 22:56 67	1/9/18 20:01 68	2/9/18 13:06 67	2/9/18 22:11 67	5/9/18 19:16 69
27/8/18 21:56 55 27/8/18 22:01 51	30/8/18 19:01 58 30/8/18 19:06 59	1/9/18 20:06 69 1/9/18 20:11 69	2/9/18 13:11 64 2/9/18 13:16 60	2/9/18 22:16 68 2/9/18 22:21 68	5/9/18 19:21 52 5/9/18 19:26 69
27/8/18 22:06 55	30/8/18 19:11 57	1/9/18 20:16 69	2/9/18 13:21 69	2/9/18 22:26 68	5/9/18 19:31 68
27/8/18 22:11 41	30/8/18 19:16 56	1/9/18 20:21 69	2/9/18 13:26 64	2/9/18 22:31 67	5/9/18 19:36 69
27/8/18 22:16 69 27/8/18 22:21 69	30/8/18 19:21 45 30/8/18 19:26 69	1/9/18 20:26 69 1/9/18 20:31 69	2/9/18 13:31 58 2/9/18 13:36 62	2/9/18 22:36 68 2/9/18 22:41 68	5/9/18 19:41 68 5/9/18 19:46 68
27/8/18 22:26 58	30/8/18 19:31 68	1/9/18 20:36 68	2/9/18 13:41 59	2/9/18 22:46 68	5/9/18 19:51 68
27/8/18 22:31 58 27/8/18 22:36 69	30/8/18 19:36 68 30/8/18 19:41 68	1/9/18 20:41 68 1/9/18 20:46 68	2/9/18 13:46 62 2/9/18 13:51 68	2/9/18 22:51 67 2/9/18 22:56 67	5/9/18 19:56 68 5/9/18 20:01 69
27/8/18 22:41 69	30/8/18 19:46 68	1/9/18 20:51 68	2/9/18 13:56 65	3/9/18 19:01 59	5/9/18 20:06 68
27/8/18 22:46 69	30/8/18 19:51 67	1/9/18 20:56 68	2/9/18 14:01 61	3/9/18 19:06 56	5/9/18 20:11 68
27/8/18 22:51 69 27/8/18 22:56 69	30/8/18 19:56 68 30/8/18 20:01 67	1/9/18 21:01 68 1/9/18 21:06 68	2/9/18 14:06 61 2/9/18 14:11 69	3/9/18 19:11 55 3/9/18 19:16 57	5/9/18 20:16 56 5/9/18 20:21 68
28/8/18 19:01 67	30/8/18 20:06 68	1/9/18 21:11 69	2/9/18 14:16 68	3/9/18 19:21 61	5/9/18 20:26 68
28/8/18 19:06 67 28/8/18 19:11 67	30/8/18 20:11 68 30/8/18 20:16 67	1/9/18 21:16 68 1/9/18 21:21 68	2/9/18 14:21 66 2/9/18 14:26 64	3/9/18 19:26 56 3/9/18 19:31 69	5/9/18 20:31 68 5/9/18 20:36 68
28/8/18 19:16 67	30/8/18 20:21 67	1/9/18 21:26 69	2/9/18 14:31 68	3/9/18 19:36 68	5/9/18 20:41 68
28/8/18 19:21 67	30/8/18 20:26 67	1/9/18 21:31 69	2/9/18 14:36 68	3/9/18 19:41 68	5/9/18 20:46 68
28/8/18 19:26 68 28/8/18 19:31 67	30/8/18 20:31 68 30/8/18 20:36 67	1/9/18 21:36 69 1/9/18 21:41 68	2/9/18 14:41 69 2/9/18 14:46 68	3/9/18 19:46 68 3/9/18 19:51 69	5/9/18 20:51 68 5/9/18 20:56 68
28/8/18 19:36 66	30/8/18 20:41 67	1/9/18 21:46 69	2/9/18 14:51 69	3/9/18 19:56 68	5/9/18 21:01 69
28/8/18 19:41 66 28/8/18 19:46 67	30/8/18 20:46 67 30/8/18 20:51 67	1/9/18 21:51 69 1/9/18 21:56 69	2/9/18 14:56 68 2/9/18 15:01 68	3/9/18 20:01 68 3/9/18 20:06 68	5/9/18 21:06 69 5/9/18 21:11 68
28/8/18 19:51 68	30/8/18 20:56 68	1/9/18 22:01 69	2/9/18 15:06 68	3/9/18 20:00 68	5/9/18 21:16 68
28/8/18 19:56 68	30/8/18 21:01 67	1/9/18 22:06 69	2/9/18 15:11 69	3/9/18 20:16 68	5/9/18 21:21 67
28/8/18 20:01 67 28/8/18 20:06 67	30/8/18 21:06 67 30/8/18 21:11 68	1/9/18 22:11 69 1/9/18 22:16 69	2/9/18 15:16 58 2/9/18 15:21 69	3/9/18 20:21 69 3/9/18 20:26 68	5/9/18 21:26 68 5/9/18 21:31 67
28/8/18 20:11 68	30/8/18 21:16 67	1/9/18 22:21 68	2/9/18 15:26 69	3/9/18 20:31 68	5/9/18 21:36 68
28/8/18 20:16 67 28/8/18 20:21 68	30/8/18 21:21 67 30/8/18 21:26 67	1/9/18 22:26 68 1/9/18 22:31 68	2/9/18 15:31 68 2/9/18 15:36 69	3/9/18 20:36 69 3/9/18 20:41 68	5/9/18 21:41 68 5/9/18 21:46 68
28/8/18 20:26 67	30/8/18 21:31 67	1/9/18 22:36 69	2/9/18 15:41 69	3/9/18 20:46 68	5/9/18 21:51 68
28/8/18 20:31 68	30/8/18 21:36 67	1/9/18 22:41 68	2/9/18 15:46 62	3/9/18 20:51 67	5/9/18 21:56 68
28/8/18 20:36 68 28/8/18 20:41 67	30/8/18 21:41 67 30/8/18 21:46 67	1/9/18 22:46 69 1/9/18 22:51 61	2/9/18 15:51 66 2/9/18 15:56 64	3/9/18 20:56 69 3/9/18 21:01 67	5/9/18 22:01 67 5/9/18 22:06 68
28/8/18 20:46 68	30/8/18 21:51 67	1/9/18 22:56 68	2/9/18 16:01 67	3/9/18 21:06 68	5/9/18 22:11 68
28/8/18 20:51 67 28/8/18 20:56 68	30/8/18 21:56 67 30/8/18 22:01 67	2/9/18 7:01 68 2/9/18 7:06 66	2/9/18 16:06 67 2/9/18 16:11 67	3/9/18 21:11 67 3/9/18 21:16 68	5/9/18 22:16 68 5/9/18 22:21 67
28/8/18 21:01 67	30/8/18 22:06 67	2/9/18 7:11 68	2/9/18 16:16 68	3/9/18 21:21 68	5/9/18 22:26 67
28/8/18 21:06 68	30/8/18 22:11 67	2/9/18 7:16 66	2/9/18 16:21 67	3/9/18 21:26 67	5/9/18 22:31 68
28/8/18 21:11 68 28/8/18 21:16 68	30/8/18 22:16 67 30/8/18 22:21 67	2/9/18 7:21 67 2/9/18 7:26 66	2/9/18 16:26 69 2/9/18 16:31 69	3/9/18 21:31 67 3/9/18 21:36 68	5/9/18 22:36 67 5/9/18 22:41 66
28/8/18 21:21 67	30/8/18 22:26 67	2/9/18 7:31 67	2/9/18 16:36 68	3/9/18 21:41 68	5/9/18 22:46 67
28/8/18 21:26 68 28/8/18 21:31 67	30/8/18 22:31 67 30/8/18 22:36 67	2/9/18 7:36 67 2/9/18 7:41 67	2/9/18 16:41 68 2/9/18 16:46 67	3/9/18 21:46 67 3/9/18 21:51 67	5/9/18 22:51 68 5/9/18 22:56 67
28/8/18 21:36 67	30/8/18 22:41 67	2/9/18 7:46 67	2/9/18 16:51 64	3/9/18 21:56 68	6/9/18 19:01 69
28/8/18 21:41 67	30/8/18 22:46 66	2/9/18 7:51 66	2/9/18 16:56 66	3/9/18 22:01 67	6/9/18 19:06 60
28/8/18 21:46 68 28/8/18 21:51 68	30/8/18 22:51 67 30/8/18 22:56 67	2/9/18 7:56 67 2/9/18 8:01 67	2/9/18 17:01 69 2/9/18 17:06 67	3/9/18 22:06 67 3/9/18 22:11 67	6/9/18 19:11 47 6/9/18 19:16 60
28/8/18 21:56 67	31/8/18 19:01 68	2/9/18 8:06 68	2/9/18 17:11 67	3/9/18 22:16 67	6/9/18 19:21 54
28/8/18 22:01 67 28/8/18 22:06 68	31/8/18 19:06 68 31/8/18 19:11 68	2/9/18 8:11 68 2/9/18 8:16 67	2/9/18 17:16 64 2/9/18 17:21 69	3/9/18 22:21 68 3/9/18 22:26 68	6/9/18 19:26 68 6/9/18 19:31 68
28/8/18 22:11 68	31/8/18 19:16 68	2/9/18 8:21 68	2/9/18 17:26 69	3/9/18 22:31 67	6/9/18 19:36 68
28/8/18 22:16 67	31/8/18 19:21 68 31/8/18 19:26 69	2/9/18 8:26 68	2/9/18 17:31 69	3/9/18 22:36 68	6/9/18 19:41 68
28/8/18 22:21 67 28/8/18 22:26 67	31/8/18 19:26 69 31/8/18 19:31 68	2/9/18 8:31 69 2/9/18 8:36 59	2/9/18 17:36 69 2/9/18 17:41 61	3/9/18 22:41 67 3/9/18 22:46 67	6/9/18 19:46 69 6/9/18 19:51 68
28/8/18 22:31 67	31/8/18 19:36 68	2/9/18 8:41 65	2/9/18 17:46 69	3/9/18 22:51 68	6/9/18 19:56 68
28/8/18 22:36 67 28/8/18 22:41 67	31/8/18 19:41 68 31/8/18 19:46 68	2/9/18 8:46 67 2/9/18 8:51 66	2/9/18 17:51 68 2/9/18 17:56 69	3/9/18 22:56 67 4/9/18 19:01 56	6/9/18 20:01 68 6/9/18 20:06 68
28/8/18 22:46 67	31/8/18 19:51 68	2/9/18 8:56 64	2/9/18 18:01 69	4/9/18 19:06 69	6/9/18 20:11 68
28/8/18 22:51 67 28/8/18 22:56 67	31/8/18 19:56 68 31/8/18 20:01 68	2/9/18 9:01 62 2/9/18 9:06 63	2/9/18 18:06 69 2/9/18 18:11 69	4/9/18 19:11 69 4/9/18 19:16 56	6/9/18 20:16 67 6/9/18 20:21 68
29/8/18 19:01 69	31/8/18 20:06 68	2/9/18 9:10 62	2/9/18 18:16 68	4/9/18 19:21 65	6/9/18 20:26 68
29/8/18 19:06 69	31/8/18 20:11 68	2/9/18 9:16 60	2/9/18 18:21 69	4/9/18 19:26 69	6/9/18 20:31 68
29/8/18 19:11 68 29/8/18 19:16 68	31/8/18 20:16 68 31/8/18 20:21 68	2/9/18 9:21 57 2/9/18 9:26 41	2/9/18 18:26 69 2/9/18 18:31 61	4/9/18 19:31 68 4/9/18 19:36 68	6/9/18 20:36 68 6/9/18 20:41 68
29/8/18 19:21 69	31/8/18 20:26 68	2/9/18 9:31 61	2/9/18 18:36 68	4/9/18 19:41 69	6/9/18 20:46 68
29/8/18 19:26 69 29/8/18 19:31 68	31/8/18 20:31 68 31/8/18 20:36 68	2/9/18 9:36 62 2/9/18 9:41 54	2/9/18 18:41 68 2/9/18 18:46 68	4/9/18 19:46 68 4/9/18 19:51 68	6/9/18 20:51 68 6/9/18 20:56 67
29/8/18 19:36 67	31/8/18 20:41 68	2/9/18 9:46 62	2/9/18 18:51 68	4/9/18 19:56 68	6/9/18 21:01 67
29/8/18 19:41 68 29/8/18 19:46 68	31/8/18 20:46 68 31/8/18 20:51 69	2/9/18 9:51 58 2/9/18 9:56 56	2/9/18 18:56 68 2/9/18 19:01 68	4/9/18 20:01 68 4/9/18 20:06 69	6/9/18 21:06 68 6/9/18 21:11 69
29/8/18 19:51 68	31/8/18 20:56 69	2/9/18 10:01 53	2/9/18 19:06 68	4/9/18 20:11 68	6/9/18 21:16 68
29/8/18 19:56 68	31/8/18 21:01 68	2/9/18 10:06 60	2/9/18 19:11 69	4/9/18 20:16 68	6/9/18 21:21 68
29/8/18 20:01 69 29/8/18 20:06 68	31/8/18 21:06 68 31/8/18 21:11 68	2/9/18 10:11 69 2/9/18 10:16 69	2/9/18 19:16 68 2/9/18 19:21 53	4/9/18 20:21 67 4/9/18 20:26 67	6/9/18 21:26 68 6/9/18 21:31 68
29/8/18 20:11 69	31/8/18 21:16 68	2/9/18 10:21 69	2/9/18 19:26 69	4/9/18 20:31 68	6/9/18 21:36 68
29/8/18 20:16 67 29/8/18 20:21 68	31/8/18 21:21 69 31/8/18 21:26 68	2/9/18 10:26 56 2/9/18 10:31 57	2/9/18 19:31 68 2/9/18 19:36 69	4/9/18 20:36 68 4/9/18 20:41 67	6/9/18 21:41 67 6/9/18 21:46 68
29/8/18 20:26 69	31/8/18 21:31 68	2/9/18 10:36 58	2/9/18 19:41 68	4/9/18 20:46 67	6/9/18 21:51 67
29/8/18 20:31 68	31/8/18 21:36 68	2/9/18 10:41 62	2/9/18 19:46 68	4/9/18 20:51 68	6/9/18 21:56 68
29/8/18 20:36 68 29/8/18 20:41 67	31/8/18 21:41 68 31/8/18 21:46 69	2/9/18 10:46 69 2/9/18 10:51 69	2/9/18 19:51 68 2/9/18 19:56 68	4/9/18 20:56 68 4/9/18 21:01 67	6/9/18 22:01 68 6/9/18 22:06 67
29/8/18 20:46 67	31/8/18 21:51 68	2/9/18 10:56 69	2/9/18 20:01 68	4/9/18 21:06 68	6/9/18 22:11 69
29/8/18 20:51 68 29/8/18 20:56 68	31/8/18 21:56 68 31/8/18 22:01 68	2/9/18 11:01 68 2/9/18 11:06 69	2/9/18 20:06 68 2/9/18 20:11 68	4/9/18 21:11 68 4/9/18 21:16 68	6/9/18 22:16 69 6/9/18 22:21 68
29/8/18 21:01 67	31/8/18 22:06 68	2/9/18 11:11 69	2/9/18 20:16 68	4/9/18 21:21 67	6/9/18 22:26 68
29/8/18 21:06 68	31/8/18 22:11 69	2/9/18 11:16 68	2/9/18 20:21 52	4/9/18 21:26 67	6/9/18 22:31 68 6/9/18 22:36 68
29/8/18 21:11 68 29/8/18 21:16 68	31/8/18 22:16 69 31/8/18 22:21 69	2/9/18 11:21 68 2/9/18 11:26 68	2/9/18 20:26 68 2/9/18 20:31 68	4/9/18 21:31 68 4/9/18 21:36 68	6/9/18 22:36 68 6/9/18 22:41 68
29/8/18 21:21 68	31/8/18 22:26 53	2/9/18 11:31 68	2/9/18 20:36 68	4/9/18 21:41 68	6/9/18 22:46 68
29/8/18 21:26 68 29/8/18 21:31 68	31/8/18 22:31 69 31/8/18 22:36 68	2/9/18 11:36 68 2/9/18 11:41 69	2/9/18 20:41 68 2/9/18 20:46 68	4/9/18 21:46 67 4/9/18 21:51 67	6/9/18 22:51 68 6/9/18 22:56 67
29/8/18 21:36 68	31/8/18 22:41 69	2/9/18 11:46 68	2/9/18 20:51 68	4/9/18 21:56 68	7/9/18 19:01 68
29/8/18 21:41 68 29/8/18 21:46 68	31/8/18 22:46 68 31/8/18 22:51 69	2/9/18 11:51 69 2/9/18 11:56 69	2/9/18 20:56 68 2/9/18 21:01 68	4/9/18 22:01 67 4/9/18 22:06 68	7/9/18 19:06 68 7/9/18 19:11 68
29/8/18 21:51 68	31/8/18 22:56 68	2/9/18 12:01 69	2/9/18 21:06 68	4/9/18 22:11 67	7/9/18 19:16 68
29/8/18 21:56 68	1/9/18 19:01 69	2/9/18 12:06 69	2/9/18 21:11 68	4/9/18 22:16 68	7/9/18 19:21 68

	Real-time Noise 7/9/18 19:26 7/9/18 19:31	68 67	RTN1 (Food and Environ 9/9/18 8:31 68 9/9/18 8:36 69	9/9/18 17:36 9/9/18 17:41	68 69	10/9/18 22:41 68 10/9/18 22:46 68		6715/9/18 20:51686715/9/18 20:5668
						11/9/18 19:06 68	13/9/18 20:11	69 15/9/18 21:16 68
						11/9/18 19:26 68		68 15/9/18 21:36 68
	7/9/18 20:31	68	9/9/18 9:36 69	9/9/18 18:41	68	11/9/18 19:46 67	13/9/18 20:51	69 15/9/18 21:56 68
	7/9/18 20:51	68	9/9/18 9:56 69	9/9/18 19:01	68	11/9/18 20:06 68	13/9/18 21:11	68 15/9/18 22:16 68
Think 2000 Boy No 101 Boy No 101 Boy No 100 Boy No 1000 Boy No								
Table 1241 Boy Boyle 1002 Boyle 1002 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>13/9/18 21:31</td> <td>68 15/9/18 22:36 68</td>							13/9/18 21:31	68 15/9/18 22:36 68
Trinte 2.06 Bayles (10.5) Best Unite 1.06 Inite 2.06 Bayles (10.5) Best Inite 2.06 Bayles (10.5) Bayles (10.								
Trint 2113 BB Delta 10.4 BB 11010 20.46 BB 15010 22.15								
The Part of the Set Set 10 (1) Set 10 (1) <t< td=""><td>7/9/18 21:31</td><td>68</td><td>9/9/18 10:36 68</td><td>9/9/18 19:41</td><td>68</td><td>11/9/18 20:46 68</td><td>13/9/18 21:51</td><td>68 15/9/18 22:56 68</td></t<>	7/9/18 21:31	68	9/9/18 10:36 68	9/9/18 19:41	68	11/9/18 20:46 68	13/9/18 21:51	68 15/9/18 22:56 68
Trink 1.1.4 Boy 1.1.5								
7.14 1.14 0.0 </td <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>								
Trans 2001 Ge Marks 105 Ge Marks 2011 Ge Trans 2014 Ge <thtrans 2014<="" th=""> Ge <thtrans 2014<="" td=""><td>7/9/18 21:51</td><td></td><td>9/9/18 10:56 68</td><td>9/9/18 20:01</td><td>68</td><td>11/9/18 21:06 68</td><td>13/9/18 22:11</td><td>68 16/9/18 7:16 68</td></thtrans></thtrans>	7/9/18 21:51		9/9/18 10:56 68	9/9/18 20:01	68	11/9/18 21:06 68	13/9/18 22:11	68 16/9/18 7:16 68
Trans 2006 Gel Mark 8111 Gel Mark 82116 Gel Trans 82216 Gel Trans 8216 Gel <thtrans 8216<="" th=""> <thtrans 8216<="" th=""></thtrans></thtrans>								
Trans 22:11 Ge Self 11:16 Self 12:16 Self 12:16 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>								
The full sector Best Billing Best Billi			9/9/18 11:16 68		67			69 16/9/18 7:36 68
TMM E2246 68 MM E 2046 MM E 2								
7.3h12.2.2.1 66 9.4h12.2.1.1 68 11.5h12.2.4 68 13.3h12.2.5.1 66 15.6h17.5.5 67 7.3h12.2.2.4 68 9.9h12.0.5.4 68 11.5h12.2.5.1 68 13.3h12.2.5.1 68 15.6h17.5.5								
TAYLE 2241 68 MUTE 11146 69 MUTE 2251 68 HAURE 1001 68 HEME 805 60 TAYLE 2244 68 MUTE 1156 60 MUTE 2211 66 HAURE 2211 66 HAURE 1010 68 HEME 805 60 HAURE 2211 66 HAURE 1010 68 HEME 821 66 HAURE 1010 68 HEME 805 68 HAURE 1010 68 HEME 805 60 HAURE 805 <t< td=""><td>7/9/18 22:31</td><td></td><td>9/9/18 11:36 69</td><td>9/9/18 20:41</td><td></td><td>11/9/18 21:46 68</td><td>13/9/18 22:51</td><td>68 16/9/18 7:56 68</td></t<>	7/9/18 22:31		9/9/18 11:36 69	9/9/18 20:41		11/9/18 21:46 68	13/9/18 22:51	68 16/9/18 7:56 68
TM-112.2246 68 99/18 11:51 68 99/18 22:56 68 119/18 22:56 68 149/18 12:51								
7.9412.2521 68 99/181155 69 99/12101 66 11/9/18.2016 68 14/9/18.1016 68 16/9/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.101 68 99/18.102 68 11/9/18.221 69 14/9/18.102 68 14/9/18.102 69 14/9/18.102 16 16/9/18.101 16/9/18.101<								
Bind Bind Ge Bind Bind Ge Bind Bind Ge Link Bind Ge Li								
Bind Binds 68 90/18 12:11 68 90/18 12:15 69 110/18 22:15 69 140/18 13:16 69 150/18 83:16 67 Bind Bind Line 69 90/18 12:26 60 110/18 22:25 60 140/18 13:16 60 160/18 83:16 60 Bind Bind 68 90/18 12:26 60 140/18 12:26 60 140/18 12:36 60 140/18 12:36 60 160/18 83:16 61 Bind Bind 68 90/18 12:36 60 140/18 12:31 <								
Bight Bight Bight Bight Bight <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>								
Bind Big21 66 10/018 22:56 66 11/018 22:56 66 14/018 19:44 67 15/018:46 15/018:46 Bind Big21 66 90/018 12:40 66 11/018 22:51 68 14/018 19:44 68 14/018 19:44 68 14/018 19:44 68 14/018 19:44 68 14/018 19:44 68 14/018 22:51 68 14/018 20:01 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 16/018 90:16 68 14/018 20:26 68 16/018 90:16 68 14/018 20:26 68 16/018 90:16 68 14/018 20:16 68 16/018 90:16 68 14/018 20:16 68 16/018 90:16 68 16/018 90:16 68 16/0								68 16/9/18 8:36 67
8/14 8/14 11/14 8/24 11/47/8 8/24 11/47/8 8/24 11/47/8 8/24 11/47/8 8/24 11/47/8 8/24 11/47/8 8/24 11/47/8 8/24 11/47/8 8/24 6/24 6/24 11/47/8 8/24 6/24 6/24 6/24 6/24 6/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 6/24 11/47/8 8/24 8/24 8/24 8/								
8)9/16 9/9/18 1/16 1/16 2/2.4 63 1/16/18 2/2.4 63 1/16/18 2/2.4 63 1/16/18 62/2 63 1/16/18 62/2 63 1/16/18 62/2 1/16/18 62/2 1/16/18 62/2 1/16/18 62/2 1/16/18 62/2 1/16/18 62/2 1/16/18 62/2 1/16/18 62/2 1/16/18 62/2 1/16/18 62/2 1/16/18 <t< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>								
Byns Byns <th< td=""><td>8/9/18 19:31</td><td>68</td><td>9/9/18 12:36 69</td><td>9/9/18 21:41</td><td>63</td><td>11/9/18 22:46 63</td><td>14/9/18 19:51</td><td>68 16/9/18 8:56 67</td></th<>	8/9/18 19:31	68	9/9/18 12:36 69	9/9/18 21:41	63	11/9/18 22:46 63	14/9/18 19:51	68 16/9/18 8:56 67
Byrk 1946 69 94/18 12:15 69 94/18 12:15 69 12/18 19:01 69 14/19 8 2016 68 16/11 8 21 66 8/19 14 19:51 69 94/18 22:01 63 12/018 19:01 69 14/19 8 2011 68 16/018 22:1 63 12/018 19:01 69 14/018 20:0 68 16/018 22:1 63 12/018 19:02 69 14/018 20:0 68 16/018 32:1 63 12/018 19:22 60 12/018 19:23 68 14/018 20:0 69 16/018 32:8 69 16/018 32:8 68 14/018 20:0 69 16/018 32:8 69 12/018 19:23 68 14/018 20:0 69 16/018 32:8 69 12/018 19:23 68 14/018 20:0 69 16/018 32:8 69 12/018 19:25 68 14/018 20:0 69 16/018 19:2 69 16/018 19:2 69 16/018 19:2 69 16/018 19:1 60 16/018 19:1 60 16/018 19:1 60 16/018 10:1 60 16/018 10:1 60 16/018 10:1 60 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>								
Birls 1951 69 90/18 12:0 63 12/9/18 19:0 69 14/9/18 20:1 68 16/9/18 9:1 63 Birls 20:01 63 90/18 22:0 63 12/9/18 19:16 64 14/9/18 20:16 68 16/9/18 20:1 63 Birls 20:01 63 90/18 22:11 63 12/9/18 19:16 63 14/9/18 20:1 63 16/9/18 10:1 64 16/9/18 20:1 63								
Big Hig 20:01 69 99/H 8 32:16 69 99/H 8 22:16 69 14/5/H 8 22:17 68 14/5/H 8 22:16 68 14/5/H 8 2:16 68 14/5/H 8 2	8/9/18 19:51	69	9/9/18 12:56 69	9/9/18 22:01	63	12/9/18 19:06 69	14/9/18 20:11	68 16/9/18 9:16 67
By/H 20206 68 99/9/H 31:16 69 99/9/H 32:16 68 129/18 19:26 69 149/18 20:26 55 169/18 93:16 68 By/H 20211 68 99/07 8 13:16 68 99/07 8 22:26 60 129/11 19:26 69 149/18 20:31 69 169/18 93:16 69 169/18 93:16 69 169/18 93:16 69 169/18 93:16 69 169/18 93:16 69 169/18 93:16 69 169/18 93:16 69 169/18 93:16 69 169/18 93:16 69 169/18 93:6 68 169/18 19:36 68 169/18 19:36 68 169/18 19:36 68 169/18 19:36 68 169/18 19:36 68 169/18 19:36 68 169/18 19:36 68 169/18 19:36 68 109/18 19:36 68 109/18 19:36 68 109/18 19:36 68 109/18 19:36 68 109/18 19:36 68 109/18 19:36 68 109/18 19:36 68 109/18 19:36 68 109/18 19:36 68 169/18 19:36 68 169/18 19:36 68 169/18								
Byn18 20:11 68 99/18 13:26 68 99/18 22:21 60 12/18 13:26 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 69 14/97 8 20:36 68 14/97 8 20:36 68 14/97 8 20:36 68 14/97 8 20:36 68 14/97 8 20:36 68 14/97 8 20:36 68 14/97 8 20:36 68 14/97 8 20:36 68 14/97 8 20:37 68 14/97 8 20:36 68 14/97 8 20:37 68 14/97 8 20:37 68 14/97 8 20:37 68 14/97 8 20:37 68 14/97 8 20:37 68 14/97 8 20:37 68 14/97 8 20:37 69 14/97 8 20:37 69 14/97 8 20:37 69 14/97 8 20:37 69 14/97 8 20:37 69 14/97 8 20:37 69 14/97 8 20:37 69 14/97 8 20:37 69								
Birls Bozh 68 14/9/18 20:41 69 16/9/18 20:36 68 14/9/18 20:44 68 14/9/18 20:44 68 14/9/18 20:46 68 16/9/18 10:30 68 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td>69 16/9/18 9:36 68</td>								69 16/9/18 9:36 68
8/9/18 20:26 67 9/9/18 13:31 67 9/9/18 22:36 68 12/9/18 19:46 68 14/9/18 20:45 68 16/9/18 55:5 68 8/9/18 20:36 68 9/9/18 13:41 68 9/9/18 22:45 68 12/9/18 19:46 68 14/9/18 20:55 69 16/9/18 50:56 69 16/9/18 10:06 60 9/9/18 20:51 68 9/9/18 13:56 68 9/9/18 13:56 68 9/9/18 13:56 68 9/9/18 13:56 68 9/9/18 13:56 68 9/9/18 13:56 68 9/9/18 13:56 68 9/9/18 13:56 68 9/9/18 14:56 68 16/9/18 10:16 69 12/9/18 20:11 68 14/9/18 21:26 69 16/9/18 10:21 68 9/9/18 14:46 68 10/9/18 19:15 55 12/9/18 20:21 68 14/9/18 21:36 69 16/9/18 10:21 68 14/9/18 21:36 69 16/9/18 10:24 68 14/9/18 21:36 69 16/9/18 10:24 68 14/9/18 21:36 69 16/9/18 10:36 68 14/9/18 21:36 69								
99/18 (2):46 68 99/18 (2):45 68 14/9/18 (2):56 69 14/9/18 (2):56 69 14/9/18 (2):56 69 14/9/18 (2):56 69 16/9/18 (1):16 69 <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>								
ByB18 22:41 66 9/9/18 12:46 66 12/9/18 20:51 66 14/9/18 21:01 69 16/9/18 10:01 60 ByB18 20:51 66 9/9/18 13:56 68 10/9/18 19:01 69 12/9/18 20:06 68 14/9/18 21:11 68 16/9/18 10:11 66 ByB18 20:51 68 9/9/18 13:56 68 10/9/18 19:01 69 12/9/18 20:06 68 14/9/18 21:11 68 16/9/18 10:21 68 ByB18 21:16 68 9/9/18 14:16 68 10/9/18 19:21 57 12/9/18 20:21 68 14/9/18 21:31 69 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:31 68 16/9/18 10:35 68 14/9/18 21:36 69 16/9/18 10:41 50 16/9/18 10:41 50 16/9/18 10:41 50 16/9/18 10:41 50 16/9/18 10:41 50								
Big 18 20:46 66 99/91 81 25:1 66 99/91 82:56 66 12/91 82:00 68 14/91 82:10 69 16/91 81:01 60 80/91 82:05 66 99/91 81:05 66 12/91 82:00 68 14/91 82:11 69 16/91 81:01 66 14/91 82:12 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 14/91 82:14 69 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68 16/91 81:01 68								
9/9/18 20:56 66 9/9/18 14:01 69 12/9/18 20:11 69 14/9/18 21:16 69 16/9/18 10:21 68 8/9/18 21:06 68 9/9/18 14:11 69 10/9/18 19:16 55 12/9/18 20:21 68 14/9/18 21:26 69 16/9/18 10:31 69 16/9/18 10:31 69 16/9/18 10:31 69 16/9/18 10:31 69 16/9/18 10:31 69 16/9/18 10:31 69 16/9/18 10:31 69 16/9/18 10:31 69 16/9/18 10:41 68 14/9/18 21:36 68 14/9/18 21:41 69 16/9/18 10:41 68 14/9/18 21:41 69 16/9/18 10:41 68 12/9/18 20:41 68 14/9/18 21:45 69 16/9/18 10:41 68 12/9/18 20:41 68 14/9/18 21:45 69 16/9/18 10:41 68 12/9/18 20:41 68 14/9/18 21:45 69 16/9/18 10:45 68 12/9/18 20:41 68 14/9/18 21:45 69 16/9/18 11:45 69 16/9/18 11:45 69 16/9/18 11:45 69 16/9/18 11:16 12/9/18 20:51 69				9/9/18 22:56	68		14/9/18 21:06	69 16/9/18 10:11 60
99/18 99/18 14/9/18 12/9/18 20/16 68 14/9/18 21/21 68 14/9/18 12/3/18 99/18 10/18 <td< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></td<>								
8/918 9/918 11/1 68 9/918 11/1 68 14/918 21:26 69 16/918 10:36 55 8/918 21:16 68 9/918 14:21 69 10/918 12:26 59 12:9/18 20:36 68 14/918 11:36 69 16/918 10:46 68 8/918 21:26 68 9/918 14:31 68 10/918 13:36 69 12/918 20:36 68 14/918 11:36 69 16/918 10:36 66 8/918 21:36 69 9/918 14:41 68 10/918 15:36 68 12/918 20:56 67 14/918 22:56 69 16/918 11:10 66 8/918 14:51 68 9/918 14:51 68 12/918 20:16 68 14/918 22:16 58 16/918 11:11 66 8/918 14:51 68 9/918 14:51								
8/9/18 9/9/18 1/2/18 20/18 20/18 20/18 21/11 66 1/9/18 22/11 66 1/9/18 22/11 66 1/9/18 22/11 66 1/9/18 22/11 66 1/9/18 22/11 66 1/9/18 22/11 66 1/9/18 22/11 66 1/9/18 22/11 66 1/9/18 22/11 66							14/9/18 21:26	
8/918 9/918 <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>								
8/9/18 9/9/18 1/3/18 1/9/18<								
99/18 91/18 <th< td=""><td></td><td></td><td>9/9/18 14:31 68</td><td></td><td></td><td></td><td></td><td></td></th<>			9/9/18 14:31 68					
99/18 21/41 68 99/18 14/46 68 12/9/18 21/18 20/18 21/								
By/B 21:46 68 9//B 14:51 69 10/9/B 21:56 68 12/9/B 21:50 68 14/9/B 22:06 69 16/9/B 11:16 66 By/B 21:56 68 9/9/B 15:01 68 10/9/B 20:06 68 12/9/B 21:06 68 14/9/B 22:16 56 16/9/B 11:26 68 By/B 22:06 68 9/9/B 15:01 68 10/9/B 20:16 68 12/9/B 21:26 68 14/9/B 22:26 69 16/9/B 11:31 66 By/B 22:16 68 9/9/B 15:26 69 10/9/B 20:26 68 12/9/B 21:26 68 14/9/B 22:31 69 16/9/B 11:31 66 By/B 22:26 67 9/9/B 15:31 69 10/9/B 20:36 69 12/9/B 21:36 68 14/9/B 22:46 69 16/9/B 11:51 63 By/B 22:26 67 9/9/B 15:31 69 10/9/B 20:36 69 12/9/B 21:36 68 14/9/B 22:46 69 16/9/B 11:51 63 By/B 22:36 68 9/9/B 15:51 50 10/9/B 20:36 6								
$\begin{array}{rrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrr$								
9/9/18 22:06 68 9/9/18 15:11 69 10/9/18 20:16 68 12/9/18 21:21 67 14/9/18 22:26 69 16/9/18 11:31 66 8/9/18 22:16 68 9/9/18 15:21 68 10/9/18 20:26 68 12/9/18 21:31 68 14/9/18 22:36 69 16/9/18 11:34 66 8/9/18 22:26 67 9/9/18 15:31 69 10/9/18 20:26 68 12/9/18 21:31 68 14/9/18 22:41 69 16/9/18 11:34 66 8/9/18 22:26 67 9/9/18 15:31 69 10/9/18 20:41 68 14/9/18 22:41 69 16/9/18 11:51 66 8/9/18 22:36 68 9/9/18 15:31 69 10/9/18 20:46 68 12/9/18 21:41 68 14/9/18 22:51 69 16/9/18 12:01 63 8/9/18 22:46 68 9/9/18 15:51 58 10/9/18 20:56 54 12/9/18 21:56 67 15/9/18 19:01 54 16/9/18 12:16 63 15/9/18 19:01 54 16/9/18 12:16 63 15/9/18 19:11 69 16/9/18 12:16 63 16/9/18 12:16 63 16/9/18 12:16 63 15/9/				10/9/18 20:0	6 68 1 69			
8/9/18 22:16 68 10/9/18 20:26 68 12/9/18 21:31 68 14/9/18 22:36 69 16/9/18 11:41 65 8/9/18 22:26 67 9/9/18 15:31 69 10/9/18 20:31 69 12/9/18 21:31 68 14/9/18 22:46 69 16/9/18 11:51 68 8/9/18 22:26 67 9/9/18 15:31 69 10/9/18 20:31 68 12/9/18 21:44 68 14/9/18 22:46 69 16/9/18 11:51 68 8/9/18 22:36 68 9/9/18 15:46 69 10/9/18 20:46 68 12/9/18 21:56 67 15/9/18 19:01 54 16/9/18 12:01 66 8/9/18 22:41 68 9/9/18 15:51 58 10/9/18 20:56 54 12/9/18 22:01 68 15/9/18 19:01 59 16/9/18 12:21 67 8/9/18 22:46 68 9/9/18 16:01 54 10/9/18 21:01 68 12/9/18 22:01 68 15/9/18 19:11 69 16/9/18 12:21 67 8/9/18 22:56 68 9/9/18 16:01 54 10/9/18 21:11 68 </td <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>								
$\begin{array}{llllllllllllllllllllllllllllllllllll$								
8/9/18 22:31 68 9/9/18 15:36 69 10/9/18 20:41 68 12/9/18 21:46 68 14/9/18 22:51 69 16/9/18 11:50 66 8/9/18 22:41 68 9/9/18 15:46 69 10/9/18 20:51 68 12/9/18 21:56 67 15/9/18 19:01 54 16/9/18 12:01 68 8/9/18 22:46 68 9/9/18 15:51 58 10/9/18 20:56 54 12/9/18 22:01 68 15/9/18 19:01 69 16/9/18 12:16 67 8/9/18 22:56 68 9/9/18 15:01 54 10/9/18 21:01 68 12/9/18 22:11 67 15/9/18 19:01 69 16/9/18 12:21 67 9/9/18 7:01 67 9/9/18 16:01 54 10/9/18 21:16 67 12/9/18 22:11 68 15/9/18 19:21 69 16/9/18 12:26 67 9/9/18 7:06 66 9/9/18 16:21 64 10/9/18 21:26 68 15/9/18 19:31 68 16/9/18 12:26 67 9/9/18 7:16 67 9/9/18 16:21 64 10/9/18 21:36 68								
$\begin{array}{rrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrr$								
8/9/18 22:46 68 9/9/18 15:51 58 10/9/18 20:56 54 12/9/18 22:01 68 15/9/18 19:06 69 16/9/18 12:11 67 8/9/18 22:56 68 9/9/18 16:06 58 10/9/18 21:01 68 12/9/18 22:11 67 15/9/18 19:16 69 16/9/18 12:16 69 9/9/18 7:01 67 9/9/18 16:06 58 10/9/18 21:16 67 15/9/18 22:11 69 16/9/18 12:26 69 9/9/18 7:06 66 9/9/18 16:16 64 10/9/18 21:16 67 12/9/18 22:26 68 15/9/18 19:21 69 16/9/18 12:21 66 9/9/18 7:16 66 9/9/18 16:21 64 10/9/18 21:26 68 15/9/18 19:31 68 16/9/18 12:41 67 9/9/18 7:21 66 9/9/18 16:21 64 10/9/18 21:31 68 12/9/18 22:36 68 15/9/18 19:41 69 16/9/18 12:41 67 9/9/18 7:26 67 9/9/18 16:36 61 10/9/18 21:36 68 12/9/18 22:36 68								
8/9/18 22:51 68 9/9/18 15:56 69 10/9/18 21:01 68 12/9/18 22:06 68 15/9/18 19:11 69 16/9/18 12:16 67 8/9/18 22:56 68 9/9/18 16:01 54 10/9/18 21:01 68 12/9/18 22:16 68 15/9/18 19:21 69 16/9/18 12:26 67 9/9/18 7:06 66 9/9/18 16:11 54 10/9/18 21:16 67 12/9/18 22:16 68 15/9/18 19:21 69 16/9/18 12:26 67 9/9/18 7:16 66 9/9/18 16:16 64 10/9/18 21:21 68 12/9/18 22:36 68 15/9/18 19:36 54 16/9/18 12:26 67 9/9/18 7:26 67 9/9/18 16:26 64 10/9/18 21:36 68 12/9/18 22:36 68 15/9/18 19:41 69 16/9/18 12:46 67 9/9/18 7:26 67 9/9/18 16:36 61 10/9/18 21:36 68 12/9/18 22:46 67 15/9/18 19:46 68 16/9/18 12:56 67 9/9/18 7:36 67 9/9/18 16:31 56								
9/9/18 7:01 67 9/9/18 16:06 58 10/9/18 21:11 68 12/9/18 22:16 68 15/9/18 19:21 69 16/9/18 12:26 67 9/9/18 7:06 66 9/9/18 16:11 54 10/9/18 21:16 67 12/9/18 22:21 68 15/9/18 19:31 68 16/9/18 12:36 67 9/9/18 7:16 66 9/9/18 16:21 64 10/9/18 21:31 68 12/9/18 22:31 68 15/9/18 19:31 68 16/9/18 12:36 67 9/9/18 7:26 67 9/9/18 16:36 61 10/9/18 21:31 68 12/9/18 22:36 68 15/9/18 19:41 69 16/9/18 12:26 67 9/9/18 7:36 67 9/9/18 16:36 61 10/9/18 21:36 68 12/9/18 22:46 67 15/9/18 19:46 68 16/9/18 12:56 67 9/9/18 7:36 67 9/9/18 16:36 61 10/9/18 21:46 68 12/9/18 22:56 67 15/9/18 19:51 68 16/9/18 13:01 68 9/9/18 7:46 67 9/9/18 16:51 61	8/9/18 22:51	68	9/9/18 15:56 69	10/9/18 21:0	1 68	12/9/18 22:06 68	15/9/18 19:11	69 16/9/18 12:16 67
9/9/18 7:06 66 9/9/18 16:11 54 10/9/18 21:16 67 12/9/18 22:21 68 15/9/18 19:26 69 16/9/18 12:31 66 9/9/18 7:11 67 9/9/18 16:16 64 10/9/18 21:21 68 12/9/18 22:31 68 15/9/18 19:36 54 16/9/18 12:34 67 9/9/18 7:21 66 9/9/18 16:26 64 10/9/18 21:31 68 12/9/18 22:36 68 15/9/18 19:36 54 16/9/18 12:34 67 9/9/18 7:26 67 9/9/18 16:36 61 10/9/18 21:34 68 12/9/18 22:44 67 15/9/18 19:46 68 16/9/18 12:51 66 9/9/18 7:36 67 9/9/18 16:41 69 10/9/18 21:51 68 12/9/18 22:51 68 15/9/18 19:56 68 16/9/18 12:51 67 9/9/18 7:46 67 9/9/18 16:51 61 10/9/18 21:51 68 12/9/18 22:56 67 15/9/18 20:01 68 16/9/18 13:01 68 9/9/18 7:51 67 9/9/18 16:56 49								
9/9/18 7:16 66 9/9/18 16:21 64 10/9/18 21:26 68 12/9/18 22:31 68 15/9/18 19:36 54 16/9/18 12:41 67 9/9/18 7:26 67 9/9/18 16:31 56 10/9/18 21:31 68 12/9/18 22:36 68 15/9/18 19:46 68 16/9/18 12:45 56 9/9/18 7:31 67 9/9/18 16:36 61 10/9/18 21:46 68 12/9/18 22:46 67 15/9/18 19:46 68 16/9/18 12:45 66 9/9/18 7:36 67 9/9/18 16:36 61 10/9/18 21:46 68 12/9/18 22:46 67 15/9/18 19:56 68 16/9/18 12:56 67 9/9/18 7:36 67 9/9/18 16:56 61 10/9/18 21:46 68 12/9/18 22:56 67 15/9/18 20:01 68 16/9/18 13:01 66 9/9/18 7:56 67 9/9/18 16:56 49 10/9/18 22:01 68 13/9/18 19:06 68 15/9/18 20:01 68 16/9/18 13:11 66 9/9/18 7:56 67 9/9/18 17:06 69								
9/9/18 7:21 66 9/9/18 16:26 64 10/9/18 21:31 68 12/9/18 22:36 68 15/9/18 19:41 69 16/9/18 12:46 67 9/9/18 7:31 67 9/9/18 16:36 61 10/9/18 21:31 68 12/9/18 22:41 68 15/9/18 19:46 68 16/9/18 12:46 67 9/9/18 7:36 67 9/9/18 16:36 61 10/9/18 21:46 68 12/9/18 22:51 68 15/9/18 19:51 68 16/9/18 12:56 67 9/9/18 7:36 67 9/9/18 16:46 69 10/9/18 21:51 68 12/9/18 22:51 68 15/9/18 19:50 68 16/9/18 13:01 63 9/9/18 7:56 67 9/9/18 16:56 49 10/9/18 21:51 68 13/9/18 19:01 68 15/9/18 20:01 68 16/9/18 13:11 66 9/9/18 7:56 67 9/9/18 17:01 56 10/9/18 22:01 68 13/9/18 19:06 68 15/9/18 20:11 68 16/9/18 13:21 67 9/9/18 7:56 67 9/9/18 17:06 69	9/9/18 7:11	67	9/9/18 16:16 64	10/9/18 21:2	1 68	12/9/18 22:26 68	15/9/18 19:31	68 16/9/18 12:36 67
9/9/18 7:26 67 9/9/18 16:31 56 10/9/18 21:36 68 12/9/18 22:41 68 15/9/18 19:46 68 16/9/18 12:51 66 9/9/18 7:31 67 9/9/18 16:36 61 10/9/18 21:41 68 12/9/18 22:46 67 15/9/18 19:51 68 16/9/18 12:56 67 9/9/18 7:36 67 9/9/18 16:46 69 10/9/18 21:41 68 12/9/18 22:51 68 15/9/18 19:56 68 16/9/18 13:01 66 9/9/18 7:46 67 9/9/18 16:46 69 10/9/18 21:51 68 13/9/18 19:01 68 15/9/18 20:01 68 16/9/18 13:06 66 9/9/18 7:56 67 9/9/18 16:56 49 10/9/18 22:01 68 13/9/18 19:01 68 15/9/18 20:11 68 16/9/18 13:11 65 9/9/18 7:56 67 9/9/18 17:05 69 10/9/18 22:01 68 13/9/18 19:11 68 15/9/18 20:16 68 16/9/18 13:21 66 9/9/18 7:06 69 10/9/18 22:11 67								
9/9/18 7:31 67 9/9/18 16:36 61 10/9/18 21:41 68 12/9/18 22:46 67 15/9/18 19:51 68 16/9/18 12:56 67 9/9/18 7:36 67 9/9/18 16:41 69 10/9/18 21:46 68 12/9/18 22:56 67 15/9/18 19:56 68 16/9/18 13:01 66 9/9/18 7:46 67 9/9/18 16:51 61 10/9/18 21:51 68 12/9/18 22:56 67 15/9/18 20:01 68 16/9/18 13:01 66 9/9/18 7:46 67 9/9/18 16:56 49 10/9/18 21:01 68 13/9/18 19:01 68 15/9/18 20:01 68 16/9/18 13:16 66 9/9/18 7:56 67 9/9/18 16:56 49 10/9/18 22:01 68 13/9/18 19:06 68 15/9/18 20:01 68 16/9/18 13:16 66 9/9/18 7:56 67 9/9/18 17:06 69 10/9/18 22:06 68 13/9/18 19:16 69 15/9/18 20:21 68 16/9/18 13:26 67 9/9/18 8:01 68 9/9/18 17:06 69								
9/9/18 7:41 67 9/9/18 16:46 69 10/9/18 21:51 68 12/9/18 22:56 67 15/9/18 20:01 68 16/9/18 13:06 66 9/9/18 7:46 67 9/9/18 16:51 61 10/9/18 21:56 68 13/9/18 19:01 68 15/9/18 20:01 68 16/9/18 13:11 66 9/9/18 7:56 67 9/9/18 16:56 49 10/9/18 22:01 68 13/9/18 19:06 68 15/9/18 20:11 68 16/9/18 13:16 66 9/9/18 7:56 67 9/9/18 17:01 56 10/9/18 22:01 68 13/9/18 19:11 68 15/9/18 20:16 68 16/9/18 13:21 67 9/9/18 8:01 68 9/9/18 17:01 56 10/9/18 22:11 67 13/9/18 19:16 69 15/9/18 20:21 68 16/9/18 13:21 67 9/9/18 8:06 68 9/9/18 17:11 69 10/9/18 22:16 67 13/9/18 19:21 68 15/9/18 20:26 68 16/9/18 13:21 67 9/9/18 8:16 67 9/9/18 17:21 63	9/9/18 7:31	67	9/9/18 16:36 61	10/9/18 21:4	1 68	12/9/18 22:46 67	15/9/18 19:51	68 16/9/18 12:56 67
9/9/18 7:46 67 9/9/18 16:51 61 10/9/18 21:56 68 13/9/18 19:01 68 15/9/18 20:06 68 16/9/18 13:11 69 9/9/18 7:51 67 9/9/18 16:56 49 10/9/18 22:01 68 13/9/18 19:06 68 15/9/18 20:16 68 16/9/18 13:11 68 9/9/18 7:56 67 9/9/18 17:01 56 10/9/18 22:06 68 13/9/18 19:11 68 15/9/18 20:16 68 16/9/18 13:21 67 9/9/18 8:01 68 9/9/18 17:06 69 10/9/18 22:11 67 13/9/18 19:11 68 15/9/18 20:21 68 16/9/18 13:26 67 9/9/18 8:01 68 9/9/18 17:06 69 10/9/18 22:16 67 13/9/18 19:21 68 15/9/18 20:24 68 16/9/18 13:26 67 9/9/18 8:11 67 9/9/18 17:16 69 10/9/18 22:226 68 13/9/18 19:26 68 15/9/18 20:36 68 16/9/18 13:31 67 9/9/18 8:16 67 9/9/18 17:26 69								
9/9/18 7:51 67 9/9/18 16:56 49 10/9/18 22:01 68 13/9/18 19:06 68 15/9/18 20:11 68 16/9/18 13:16 66 9/9/18 7:56 67 9/9/18 17:01 56 10/9/18 22:06 68 13/9/18 19:11 68 15/9/18 20:16 68 16/9/18 13:26 67 9/9/18 8:01 68 9/9/18 17:06 69 10/9/18 22:11 67 13/9/18 19:16 69 15/9/18 20:21 68 16/9/18 13:26 67 9/9/18 8:06 68 9/9/18 17:11 69 10/9/18 22:16 67 13/9/18 19:21 68 15/9/18 20:21 68 16/9/18 13:31 67 9/9/18 8:16 67 9/9/18 17:26 69 10/9/18 22:21 68 15/9/18 20:31 68 16/9/18 13:36 67 9/9/18 8:16 67 9/9/18 17:26 69 10/9/18 22:21 68 13/9/18 19:31 66 15/9/18 20:31 68 16/9/18 13:41 67 9/9/18 8:21 54 9/9/18 17:26 69 10/9/18 22:31 68								
9/9/18 7:56 67 9/9/18 17:01 56 10/9/18 22:06 68 13/9/18 19:11 68 15/9/18 20:16 68 16/9/18 13:21 67 9/9/18 8:01 68 9/9/18 17:06 69 10/9/18 22:11 67 13/9/18 19:16 69 15/9/18 20:21 68 16/9/18 13:21 67 9/9/18 8:01 68 9/9/18 17:16 69 10/9/18 22:16 67 13/9/18 19:21 68 15/9/18 20:26 68 16/9/18 13:21 67 9/9/18 8:11 67 9/9/18 17:16 69 10/9/18 22:21 68 13/9/18 19:26 68 15/9/18 20:31 68 16/9/18 13:36 67 9/9/18 8:16 67 9/9/18 17:21 63 10/9/18 22:26 68 13/9/18 19:31 66 15/9/18 20:31 68 16/9/18 13:41 67 9/9/18 8:16 67 9/9/18 17:21 63 10/9/18 22:31 68 13/9/18 19:31 66 15/9/18 20:36 68 16/9/18 13:41 67 9/9/18 8:21 54 9/9/18 17:26 69	9/9/18 7:51	67	9/9/18 16:56 49	10/9/18 22:0	1 68	13/9/18 19:06 68	15/9/18 20:11	68 16/9/18 13:16 68
9/9/18 8:06 68 9/9/18 17:11 69 10/9/18 22:16 67 13/9/18 19:21 68 15/9/18 20:26 68 16/9/18 13:31 67 9/9/18 8:11 67 9/9/18 17:16 69 10/9/18 22:21 68 13/9/18 19:26 68 15/9/18 20:31 68 16/9/18 13:31 67 9/9/18 8:16 67 9/9/18 17:21 63 10/9/18 22:26 68 13/9/18 19:23 66 15/9/18 20:36 68 16/9/18 13:34 67 9/9/18 8:21 54 9/9/18 17:26 69 10/9/18 22:31 68 13/9/18 19:33 66 15/9/18 20:36 68 16/9/18 13:41 67 9/9/18 8:21 54 9/9/18 17:26 69 10/9/18 22:31 68 13/9/18 19:36 67 15/9/18 20:36 68 16/9/18 13:46 67	9/9/18 7:56	67	9/9/18 17:01 56	10/9/18 22:0	6 68	13/9/18 19:11 68	15/9/18 20:16	68 16/9/18 13:21 67
9/9/18 8:11 67 9/9/18 17:16 69 10/9/18 22:21 68 13/9/18 19:26 68 15/9/18 20:31 68 16/9/18 13:36 67 9/9/18 8:16 67 9/9/18 17:21 63 10/9/18 22:26 68 13/9/18 19:31 66 15/9/18 20:36 68 16/9/18 13:41 67 9/9/18 8:21 54 9/9/18 17:26 69 10/9/18 22:31 68 13/9/18 19:36 67 15/9/18 20:41 68 16/9/18 13:46 67								
9/9/18 8:16 67 9/9/18 17:21 63 10/9/18 22:26 68 13/9/18 19:31 66 15/9/18 20:36 68 16/9/18 13:41 67 9/9/18 8:21 54 9/9/18 17:26 69 10/9/18 22:31 68 13/9/18 19:36 67 15/9/18 20:41 68 16/9/18 13:46 67	9/9/18 8:11	67	9/9/18 17:16 69	10/9/18 22:2	1 68	13/9/18 19:26 68	15/9/18 20:31	68 16/9/18 13:36 67
	9/9/18 8:16	67	9/9/18 17:21 63		6 68	13/9/18 19:31 66	15/9/18 20:36	68 16/9/18 13:41 67
9/9/18 8:26 68 9/9/18 17:31 68 10/9/18 22:36 68 13/9/18 19:41 66 15/9/18 20:46 68 16/9/18 13:51 67								

16/9/18 13:56 16/9/18 14:01	<u>e Data</u> 68 67	RTN1 (Food and Environmental 17/9/18 19:01 66 17/9/18 19:06 58	19/9/18 20:06 68 19/9/18 20:11 67	21/9/18 21:11 68 21/9/18 21:16 68	23/9/18 10:16 68 23/9/18 10:21 69	23/9/18 19:21 68 23/9/18 19:26 68
16/9/18 14:06 16/9/18 14:11	67 68	17/9/18 19:11 60 17/9/18 19:16 55	19/9/18 20:16 67 19/9/18 20:21 67	21/9/18 21:21 67 21/9/18 21:26 56	23/9/18 10:26 68 23/9/18 10:31 68	23/9/18 19:31 68 23/9/18 19:36 68
16/9/18 14:16	68	17/9/18 19:21 51	19/9/18 20:26 67	21/9/18 21:31 68	23/9/18 10:36 68	23/9/18 19:41 68
16/9/18 14:21	68	17/9/18 19:26 60	19/9/18 20:31 67	21/9/18 21:36 67	23/9/18 10:41 68	23/9/18 19:46 68
16/9/18 14:26 16/9/18 14:31	68 67	17/9/18 19:31 69 17/9/18 19:36 69	19/9/18 20:36 68 19/9/18 20:41 67	21/9/18 21:41 69 21/9/18 21:46 68	23/9/18 10:46 68 23/9/18 10:51 67	23/9/18 19:51 68 23/9/18 19:56 68
16/9/18 14:36	67	17/9/18 19:41 68	19/9/18 20:46 68	21/9/18 21:51 68	23/9/18 10:56 68	23/9/18 20:01 67
16/9/18 14:41	68 67	17/9/18 19:46 68	19/9/18 20:51 68	21/9/18 21:56 68	23/9/18 11:01 68	23/9/18 20:06 67
16/9/18 14:46 16/9/18 14:51	67 67	17/9/18 19:51 68 17/9/18 19:56 68	19/9/18 20:56 68 19/9/18 21:01 68	21/9/18 22:01 68 21/9/18 22:06 68	23/9/18 11:06 68 23/9/18 11:11 68	23/9/18 20:11 67 23/9/18 20:16 68
16/9/18 14:56	67	17/9/18 20:01 68	19/9/18 21:06 68	21/9/18 22:11 69	23/9/18 11:16 68	23/9/18 20:21 67
16/9/18 15:01 16/9/18 15:06	67 66	17/9/18 20:06 68 17/9/18 20:11 68	19/9/18 21:11 68 19/9/18 21:16 68	21/9/18 22:16 68 21/9/18 22:21 68	23/9/18 11:21 68 23/9/18 11:26 67	23/9/18 20:26 68 23/9/18 20:31 68
16/9/18 15:11	67	17/9/18 20:16 68	19/9/18 21:21 67	21/9/18 22:26 68	23/9/18 11:31 67	23/9/18 20:36 68
16/9/18 15:16	67	17/9/18 20:21 68	19/9/18 21:26 67	21/9/18 22:31 68	23/9/18 11:36 68	23/9/18 20:41 68
16/9/18 15:21 16/9/18 15:26	67 67	17/9/18 20:26 68 17/9/18 20:31 68	19/9/18 21:31 66 19/9/18 21:36 67	21/9/18 22:36 68 21/9/18 22:41 67	23/9/18 11:41 68 23/9/18 11:46 68	23/9/18 20:46 68 23/9/18 20:51 68
16/9/18 15:31	69	17/9/18 20:36 68	19/9/18 21:41 67	21/9/18 22:46 67	23/9/18 11:51 68	23/9/18 20:56 67
16/9/18 15:36 16/9/18 15:41	67 69	17/9/18 20:41 68 17/9/18 20:46 68	19/9/18 21:46 66 19/9/18 21:51 67	21/9/18 22:51 68 21/9/18 22:56 67	23/9/18 11:56 68 23/9/18 12:01 67	23/9/18 21:01 67 23/9/18 21:06 68
16/9/18 15:46	68	17/9/18 20:51 68	19/9/18 21:56 68	22/9/18 19:01 68	23/9/18 12:06 68	23/9/18 21:11 68
16/9/18 15:51	68	17/9/18 20:56 68	19/9/18 22:01 68	22/9/18 19:06 67	23/9/18 12:11 69	23/9/18 21:16 68
16/9/18 15:56 16/9/18 16:01	69 69	17/9/18 21:01 68 17/9/18 21:06 69	19/9/18 22:06 68 19/9/18 22:11 68	22/9/18 19:11 68 22/9/18 19:16 69	23/9/18 12:16 68 23/9/18 12:21 68	23/9/18 21:21 68 23/9/18 21:26 68
16/9/18 16:06	68	17/9/18 21:11 68	19/9/18 22:16 68	22/9/18 19:21 67	23/9/18 12:26 69	23/9/18 21:31 68
16/9/18 16:11 16/9/18 16:16	68 67	17/9/18 21:16 68 17/9/18 21:21 68	19/9/18 22:21 68 19/9/18 22:26 67	22/9/18 19:26 68 22/9/18 19:31 68	23/9/18 12:31 69 23/9/18 12:36 69	23/9/18 21:36 68 23/9/18 21:41 68
6/9/18 16:21	69	17/9/18 21:26 68	19/9/18 22:31 68	22/9/18 19:36 68	23/9/18 12:41 68	23/9/18 21:46 68
16/9/18 16:26	67	17/9/18 21:31 68	19/9/18 22:36 67	22/9/18 19:41 68	23/9/18 12:46 69	23/9/18 21:51 68
6/9/18 16:31 6/9/18 16:36	66 64	17/9/18 21:36 68 17/9/18 21:41 68	19/9/18 22:41 68 19/9/18 22:46 67	22/9/18 19:46 68 22/9/18 19:51 68	23/9/18 12:51 68 23/9/18 12:56 69	23/9/18 21:56 69 23/9/18 22:01 67
6/9/18 16:41	68	17/9/18 21:46 69	19/9/18 22:51 67	22/9/18 19:56 68	23/9/18 13:01 69	23/9/18 22:06 68
6/9/18 16:46 6/9/18 16:51	69 66	17/9/18 21:51 69	19/9/18 22:56 68 20/9/18 19:01 68	22/9/18 20:01 68	23/9/18 13:06 68	23/9/18 22:11 67 23/9/18 22:16 68
6/9/18 16:51 6/9/18 16:56	66 66	17/9/18 21:56 69 17/9/18 22:01 69	20/9/18 19:01 68 20/9/18 19:06 68	22/9/18 20:06 67 22/9/18 20:11 67	23/9/18 13:11 68 23/9/18 13:16 68	23/9/18 22:16 68 23/9/18 22:21 68
6/9/18 17:01	67	17/9/18 22:06 69	20/9/18 19:11 68	22/9/18 20:16 68	23/9/18 13:21 68	23/9/18 22:26 68
16/9/18 17:06 16/9/18 17:11	66 66	17/9/18 22:11 69 17/9/18 22:16 69	20/9/18 19:16 68 20/9/18 19:21 68	22/9/18 20:21 68 22/9/18 20:26 68	23/9/18 13:26 67 23/9/18 13:31 68	23/9/18 22:31 67 23/9/18 22:36 68
16/9/18 17:16	67	17/9/18 22:21 69	20/9/18 19:26 68	22/9/18 20:31 69	23/9/18 13:36 67	23/9/18 22:41 68
6/9/18 17:21 6/9/18 17:26	66 66	17/9/18 22:26 68 17/9/18 22:31 69	20/9/18 19:31 67 20/9/18 19:36 66	22/9/18 20:36 68 22/9/18 20:41 68	23/9/18 13:41 68 23/9/18 13:46 68	23/9/18 22:46 67 23/9/18 22:51 67
16/9/18 17:31	68	17/9/18 22:36 69	20/9/18 19:41 65	22/9/18 20:41 68	23/9/18 13:51 67	23/9/18 22:56 69
6/9/18 17:36	66	17/9/18 22:41 69	20/9/18 19:46 66	22/9/18 20:51 69	23/9/18 13:56 68	24/9/18 19:01 69
6/9/18 17:41 6/9/18 17:46	67 67	17/9/18 22:46 68 17/9/18 22:51 69	20/9/18 19:51 67 20/9/18 19:56 68	22/9/18 20:56 69 22/9/18 21:01 68	23/9/18 14:01 67 23/9/18 14:06 67	24/9/18 19:06 68 24/9/18 19:11 68
6/9/18 17:51	65	17/9/18 22:56 68	20/9/18 20:01 68	22/9/18 21:06 67	23/9/18 14:11 67	24/9/18 19:16 68
16/9/18 17:56	66 65	18/9/18 19:01 68 18/9/18 19:06 68	20/9/18 20:06 68 20/9/18 20:11 68	22/9/18 21:11 68 22/9/18 21:16 68	23/9/18 14:16 68 23/9/18 14:21 68	24/9/18 19:21 69 24/9/18 19:26 69
6/9/18 18:01 6/9/18 18:06	65	18/9/18 19:11 68	20/9/18 20:16 68	22/9/18 21:21 68	23/9/18 14:21 68	24/9/18 19:31 69
16/9/18 18:11	65	18/9/18 19:16 69	20/9/18 20:21 67	22/9/18 21:26 68	23/9/18 14:31 68	24/9/18 19:36 68
16/9/18 18:16 16/9/18 18:21	66 65	18/9/18 19:21 69 18/9/18 19:26 56	20/9/18 20:26 68 20/9/18 20:31 68	22/9/18 21:31 68 22/9/18 21:36 68	23/9/18 14:36 68 23/9/18 14:41 68	24/9/18 19:41 68 24/9/18 19:46 69
16/9/18 18:26	67	18/9/18 19:31 68	20/9/18 20:36 68	22/9/18 21:41 67	23/9/18 14:46 68	24/9/18 19:51 69
16/9/18 18:31 16/9/18 18:36	65 65	18/9/18 19:36 69 18/9/18 19:41 67	20/9/18 20:41 67 20/9/18 20:46 68	22/9/18 21:46 68 22/9/18 21:51 67	23/9/18 14:51 68 23/9/18 14:56 68	24/9/18 19:56 67 24/9/18 20:01 67
16/9/18 18:41	66	18/9/18 19:46 68	20/9/18 20:51 67	22/9/18 21:56 67	23/9/18 15:01 68	24/9/18 20:06 68
16/9/18 18:46	65 66	18/9/18 19:51 68	20/9/18 20:56 67 20/9/18 21:01 67	22/9/18 22:01 67 22/9/18 22:06 67	23/9/18 15:06 68	24/9/18 20:11 68
16/9/18 18:51 16/9/18 18:56	66 66	18/9/18 19:56 68 18/9/18 20:01 68	20/9/18 21:01 67 20/9/18 21:06 68	22/9/18 22:06 67 22/9/18 22:11 67	23/9/18 15:11 68 23/9/18 15:16 68	24/9/18 20:16 68 24/9/18 20:21 69
16/9/18 19:01	65	18/9/18 20:06 68	20/9/18 21:11 68	22/9/18 22:16 67	23/9/18 15:21 68	24/9/18 20:26 68
6/9/18 19:06 6/9/18 19:11	65 65	18/9/18 20:11 69 18/9/18 20:16 69	20/9/18 21:16 67 20/9/18 21:21 68	22/9/18 22:21 67 22/9/18 22:26 67	23/9/18 15:26 68 23/9/18 15:31 67	24/9/18 20:31 68 24/9/18 20:36 68
6/9/18 19:16	65	18/9/18 20:21 68	20/9/18 21:26 68	22/9/18 22:31 68	23/9/18 15:36 67	24/9/18 20:41 67
6/9/18 19:21 6/9/18 19:26	65 65	18/9/18 20:26 68 18/9/18 20:31 68	20/9/18 21:31 53 20/9/18 21:36 68	22/9/18 22:36 67 22/9/18 22:41 67	23/9/18 15:41 64 23/9/18 15:46 70	24/9/18 20:46 69 24/9/18 20:51 68
16/9/18 19:31	66	18/9/18 20:36 68	20/9/18 21:41 68	22/9/18 22:41 67	23/9/18 15:51 68	24/9/18 20:56 68
6/9/18 19:36	68	18/9/18 20:41 68	20/9/18 21:46 67	22/9/18 22:51 67	23/9/18 15:56 70	24/9/18 21:01 68
6/9/18 19:41 6/9/18 19:46	68 65	18/9/18 20:46 68 18/9/18 20:51 68	20/9/18 21:51 68 20/9/18 21:56 68	22/9/18 22:56 67 23/9/18 7:01 66	23/9/18 16:01 66 23/9/18 16:06 69	24/9/18 21:06 68 24/9/18 21:11 68
6/9/18 19:51	67	18/9/18 20:56 69	20/9/18 22:01 68	23/9/18 7:06 66	23/9/18 16:11 50	24/9/18 21:16 68
6/9/18 19:56 6/9/18 20:01	66 67	18/9/18 21:01 69 18/9/18 21:06 68	20/9/18 22:06 69 20/9/18 22:11 67	23/9/18 7:11 69 23/9/18 7:16 67	23/9/18 16:16 69 23/9/18 16:21 68	24/9/18 21:21 68 24/9/18 21:26 68
6/9/18 20:01 6/9/18 20:06	68	18/9/18 21:11 68	20/9/18 22:11 67 20/9/18 22:16 68	23/9/18 7:16 67	23/9/18 16:21 68	24/9/18 21:26 68
6/9/18 20:11	67	18/9/18 21:16 68	20/9/18 22:21 68	23/9/18 7:26 67	23/9/18 16:31 71	24/9/18 21:36 69
6/9/18 20:16 6/9/18 20:21	68 66	18/9/18 21:21 68 18/9/18 21:26 69	20/9/18 22:26 45 20/9/18 22:31 68	23/9/18 7:31 67 23/9/18 7:36 68	23/9/18 16:36 70 23/9/18 16:41 61	24/9/18 21:41 68 24/9/18 21:46 68
6/9/18 20:26	66	18/9/18 21:31 68	20/9/18 22:36 68	23/9/18 7:41 67	23/9/18 16:46 69	24/9/18 21:51 68
6/9/18 20:31 6/9/18 20:36	66 66	18/9/18 21:36 68 18/9/18 21:41 68	20/9/18 22:41 67 20/9/18 22:46 67	23/9/18 7:46 67 23/9/18 7:51 68	23/9/18 16:51 73 23/9/18 16:56 72	24/9/18 21:56 67 24/9/18 22:01 68
6/9/18 20:41	66	18/9/18 21:46 68	20/9/18 22:51 68	23/9/18 7:56 68	23/9/18 17:01 71	24/9/18 22:06 68
6/9/18 20:46	66	18/9/18 21:51 68	20/9/18 22:56 68	23/9/18 8:01 68	23/9/18 17:06 69	24/9/18 22:11 69
6/9/18 20:51 6/9/18 20:56	67 67	18/9/18 21:56 68 18/9/18 22:01 69	21/9/18 19:01 68 21/9/18 19:06 68	23/9/18 8:06 68 23/9/18 8:11 68	23/9/18 17:11 69 23/9/18 17:16 71	24/9/18 22:16 52 24/9/18 22:21 69
6/9/18 21:01	67	18/9/18 22:06 68	21/9/18 19:11 68	23/9/18 8:16 68	23/9/18 17:21 64	24/9/18 22:26 69
6/9/18 21:06	66 65	18/9/18 22:11 68	21/9/18 19:16 68	23/9/18 8:21 68	23/9/18 17:26 52	24/9/18 22:31 69
6/9/18 21:11 6/9/18 21:16	65 66	18/9/18 22:16 68 18/9/18 22:21 68	21/9/18 19:21 68 21/9/18 19:26 69	23/9/18 8:26 68 23/9/18 8:31 68	23/9/18 17:31 68 23/9/18 17:36 69	24/9/18 22:36 69 24/9/18 22:41 69
6/9/18 21:21	65	18/9/18 22:26 68	21/9/18 19:31 68	23/9/18 8:36 68	23/9/18 17:41 60	24/9/18 22:46 69
6/9/18 21:26 6/9/18 21:31	66 66	18/9/18 22:31 68 18/9/18 22:36 67	21/9/18 19:36 67 21/9/18 19:41 67	23/9/18 8:41 69 23/9/18 8:46 68	23/9/18 17:46 63 23/9/18 17:51 69	24/9/18 22:51 69 24/9/18 22:56 68
6/9/18 21:36	69	18/9/18 22:41 69	21/9/18 19:46 67	23/9/18 8:51 68	23/9/18 17:56 68	25/9/18 7:01 67
16/9/18 21:41	66	18/9/18 22:46 68	21/9/18 19:51 68	23/9/18 8:56 68	23/9/18 18:01 67	25/9/18 7:06 67
16/9/18 21:46 16/9/18 21:51	66 66	18/9/18 22:51 68 18/9/18 22:56 67	21/9/18 19:56 68 21/9/18 20:01 68	23/9/18 9:01 68 23/9/18 9:06 68	23/9/18 18:06 68 23/9/18 18:11 68	25/9/18 7:11 68 25/9/18 7:16 67
16/9/18 21:56	66	19/9/18 19:01 68	21/9/18 20:06 68	23/9/18 9:11 68	23/9/18 18:16 68	25/9/18 7:21 67
6/9/18 22:01	66 66	19/9/18 19:06 68	21/9/18 20:11 68	23/9/18 9:16 69	23/9/18 18:21 68	25/9/18 7:26 67
6/9/18 22:06 6/9/18 22:11	66 66	19/9/18 19:11 68 19/9/18 19:16 68	21/9/18 20:16 68 21/9/18 20:21 67	23/9/18 9:21 68 23/9/18 9:26 68	23/9/18 18:26 68 23/9/18 18:31 68	25/9/18 7:31 67 25/9/18 7:36 67
6/9/18 22:16	66	19/9/18 19:21 68	21/9/18 20:26 68	23/9/18 9:31 68	23/9/18 18:36 68	25/9/18 7:41 68
6/9/18 22:21 6/9/18 22:26	67 66	19/9/18 19:26 68 19/9/18 19:31 67	21/9/18 20:31 68 21/9/18 20:36 68	23/9/18 9:36 69 23/9/18 9:41 68	23/9/18 18:41 68 23/9/18 18:46 68	25/9/18 7:46 67 25/9/18 7:51 68
6/9/18 22:26	66	19/9/18 19:31 67	21/9/18 20:36 68	23/9/18 9:41 68	23/9/18 18:51 68	25/9/18 7:56 67
6/9/18 22:36	65	19/9/18 19:41 68	21/9/18 20:46 68	23/9/18 9:51 68	23/9/18 18:56 68	25/9/18 8:01 67
6/9/18 22:41	66 65	19/9/18 19:46 67 19/9/18 19:51 67	21/9/18 20:51 68 21/9/18 20:56 68	23/9/18 9:56 67 23/9/18 10:01 69	23/9/18 19:01 60 23/9/18 19:06 68	25/9/18 8:06 68 25/9/18 8:11 67
16/9/18 22:46 16/9/18 22:51 16/9/18 22:56	67 65	19/9/18 19:56 66 19/9/18 20:01 67	21/9/18 21:01 68 21/9/18 21:06 68	23/9/18 10:06 68 23/9/18 10:11 69	23/9/18 19:11 68 23/9/18 19:16 68	25/9/18 8:16 68 25/9/18 8:21 68

Real-time Noise Data 25/9/18 8:26 67	RTN1 (Food and Environmental H 25/9/18 17:31 69	Hygiene Department Depot) 26/9/18 22:36 68	28/8/18 0:26 65	29/8/18 1:31 57	30/8/18 2:36 57
25/9/18 8:31 67	25/9/18 17:36 68	26/9/18 22:41 68	28/8/18 0:31 65	29/8/18 1:36 53	30/8/18 2:41 52
25/9/18 8:36 67 25/9/18 8:41 68	25/9/18 17:41 68 25/9/18 17:46 69	26/9/18 22:46 68 26/9/18 22:51 68	28/8/18 0:36 64 28/8/18 0:41 66	29/8/18 1:41 57 29/8/18 1:46 54	30/8/18 2:46 50 30/8/18 2:51 58
25/9/18 8:46 68	25/9/18 17:51 68	26/9/18 22:56 68	28/8/18 0:46 72	29/8/18 1:51 55	30/8/18 2:56 50
25/9/18 8:51 67 25/9/18 8:56 68	25/9/18 17:56 68 25/9/18 18:01 69	Night time: 23:00-07:00	28/8/18 0:51 74 28/8/18 0:56 70	29/8/18 1:56 52 29/8/18 2:01 55	30/8/18 3:01 62 30/8/18 3:06 62
25/9/18 9:01 68	25/9/18 18:06 68	<u>Night time. 23.00-07.00</u>	28/8/18 1:01 68	29/8/18 2:06 53	30/8/18 3:11 55
25/9/18 9:06 68	25/9/18 18:11 68	27/8/18 0:01 68	28/8/18 1:06 72	29/8/18 2:11 58	30/8/18 3:16 51
25/9/18 9:11 67 25/9/18 9:16 67	25/9/18 18:16 68 25/9/18 18:21 68	27/8/18 0:06 66 27/8/18 0:11 67	28/8/18 1:11 69 28/8/18 1:16 66	29/8/18 2:16 53 29/8/18 2:21 43	30/8/18 3:21 50 30/8/18 3:26 61
25/9/18 9:21 66	25/9/18 18:26 68	27/8/18 0:16 66	28/8/18 1:21 67	29/8/18 2:26 55	30/8/18 3:31 52
25/9/18 9:26 67 25/9/18 9:31 66	25/9/18 18:31 68 25/9/18 18:36 68	27/8/18 0:21 67 27/8/18 0:26 67	28/8/18 1:26 67 28/8/18 1:31 65	29/8/18 2:31 50 29/8/18 2:36 62	30/8/18 3:36 61 30/8/18 3:41 57
25/9/18 9:36 66	25/9/18 18:41 68	27/8/18 0:31 66	28/8/18 1:36 63	29/8/18 2:41 62	30/8/18 3:46 50
25/9/18 9:41 68 25/9/18 9:46 67	25/9/18 18:46 69 25/9/18 18:51 68	27/8/18 0:36 66 27/8/18 0:41 66	28/8/18 1:41 64 28/8/18 1:46 62	29/8/18 2:46 50 29/8/18 2:51 61	30/8/18 3:51 47 30/8/18 3:56 62
25/9/18 9:51 67	25/9/18 18:56 68	27/8/18 0:46 65	28/8/18 1:51 64	29/8/18 2:56 61	30/8/18 4:01 60
25/9/18 9:56 67	25/9/18 19:01 68	27/8/18 0:51 65 27/8/18 0:56 64	28/8/18 1:56 63	29/8/18 3:01 61 29/8/18 3:06 51	30/8/18 4:06 62
25/9/18 10:01 66 25/9/18 10:06 65	25/9/18 19:06 68 25/9/18 19:11 68	27/8/18 0:56 64 27/8/18 1:01 62	28/8/18 2:01 63 28/8/18 2:06 62	29/8/18 3:06 51 29/8/18 3:11 50	30/8/18 4:11 62 30/8/18 4:16 61
25/9/18 10:11 66	25/9/18 19:16 67	27/8/18 1:06 64	28/8/18 2:11 62	29/8/18 3:16 62	30/8/18 4:21 61
25/9/18 10:16 68 25/9/18 10:21 69	25/9/18 19:21 68 25/9/18 19:26 68	27/8/18 1:11 63 27/8/18 1:16 63	28/8/18 2:16 62 28/8/18 2:21 61	29/8/18 3:21 61 29/8/18 3:26 61	30/8/18 4:26 61 30/8/18 4:31 61
25/9/18 10:26 68	25/9/18 19:31 67	27/8/18 1:21 63	28/8/18 2:26 62	29/8/18 3:31 50	30/8/18 4:36 62
25/9/18 10:31 68 25/9/18 10:36 69	25/9/18 19:36 67 25/9/18 19:41 68	27/8/18 1:26 62 27/8/18 1:31 62	28/8/18 2:31 62 28/8/18 2:36 61	29/8/18 3:36 68 29/8/18 3:41 66	30/8/18 4:41 40 30/8/18 4:46 62
25/9/18 10:41 69	25/9/18 19:46 68	27/8/18 1:36 62	28/8/18 2:41 61	29/8/18 3:46 60	30/8/18 4:51 48
25/9/18 10:46 68 25/9/18 10:51 68	25/9/18 19:51 67 25/9/18 19:56 68	27/8/18 1:41 62 27/8/18 1:46 62	28/8/18 2:46 62 28/8/18 2:51 62	29/8/18 3:51 55 29/8/18 3:56 55	30/8/18 4:56 61 30/8/18 5:01 52
25/9/18 10:56 69	25/9/18 20:01 67	27/8/18 1:51 63	28/8/18 2:56 62	29/8/18 4:01 62	30/8/18 5:06 61
25/9/18 11:01 69	25/9/18 20:06 67	27/8/18 1:56 62	28/8/18 3:01 67	29/8/18 4:06 62	30/8/18 5:11 62
25/9/18 11:06 68 25/9/18 11:11 69	25/9/18 20:11 68 25/9/18 20:16 68	27/8/18 2:01 63 27/8/18 2:06 63	28/8/18 3:06 69 28/8/18 3:11 66	29/8/18 4:11 61 29/8/18 4:16 62	30/8/18 5:16 54 30/8/18 5:21 56
25/9/18 11:16 68	25/9/18 20:21 67	27/8/18 2:11 61	28/8/18 3:16 61	29/8/18 4:21 43	30/8/18 5:26 56
25/9/18 11:21 68 25/9/18 11:26 57	25/9/18 20:26 68 25/9/18 20:31 68	27/8/18 2:16 61 27/8/18 2:21 62	28/8/18 3:21 49 28/8/18 3:26 60	29/8/18 4:26 62 29/8/18 4:31 61	30/8/18 5:31 50 30/8/18 5:36 56
25/9/18 11:31 68	25/9/18 20:36 68	27/8/18 2:26 62	28/8/18 3:31 62	29/8/18 4:36 61	30/8/18 5:41 56
25/9/18 11:36 69 25/9/18 11:41 68	25/9/18 20:41 68 25/9/18 20:46 67	27/8/18 2:31 63 27/8/18 2:36 62	28/8/18 3:36 53 28/8/18 3:41 62	29/8/18 4:41 62 29/8/18 4:46 62	30/8/18 5:46 61 30/8/18 5:51 60
25/9/18 11:46 68	25/9/18 20:51 67	27/8/18 2:41 63	28/8/18 3:46 61	29/8/18 4:51 46	30/8/18 5:56 61
25/9/18 11:51 68 25/9/18 11:56 69	25/9/18 20:56 67 25/9/18 21:01 68	27/8/18 2:46 62 27/8/18 2:51 62	28/8/18 3:51 61	29/8/18 4:56 62 29/8/18 5:01 61	30/8/18 6:01 60
25/9/18 12:01 69	25/9/18 21:01 68 25/9/18 21:06 68	27/8/18 2:51 62 27/8/18 2:56 62	28/8/18 3:56 52 28/8/18 4:01 62	29/8/18 5:06 62	30/8/18 6:06 62 30/8/18 6:11 62
25/9/18 12:06 69	25/9/18 21:11 68	27/8/18 3:01 62	28/8/18 4:06 58	29/8/18 5:11 50	30/8/18 6:16 64
25/9/18 12:11 68 25/9/18 12:16 69	25/9/18 21:16 67 25/9/18 21:21 68	27/8/18 3:06 62 27/8/18 3:11 61	28/8/18 4:11 64 28/8/18 4:16 60	29/8/18 5:16 57 29/8/18 5:21 50	30/8/18 6:21 64 30/8/18 6:26 65
25/9/18 12:21 69	25/9/18 21:26 68	27/8/18 3:16 61	28/8/18 4:21 57	29/8/18 5:26 57	30/8/18 6:31 65
25/9/18 12:26 55 25/9/18 12:31 69	25/9/18 21:31 67 25/9/18 21:36 68	27/8/18 3:21 62 27/8/18 3:26 61	28/8/18 4:26 58 28/8/18 4:31 61	29/8/18 5:31 48 29/8/18 5:36 57	30/8/18 6:36 65 30/8/18 6:41 66
25/9/18 12:36 69	25/9/18 21:41 68	27/8/18 3:31 62	28/8/18 4:36 61	29/8/18 5:41 58	30/8/18 6:46 66
25/9/18 12:41 69 25/9/18 12:46 69	25/9/18 21:46 68 25/9/18 21:51 68	27/8/18 3:36 62 27/8/18 3:41 61	28/8/18 4:41 62 28/8/18 4:46 47	29/8/18 5:46 60 29/8/18 5:51 58	30/8/18 6:51 66 30/8/18 6:56 66
25/9/18 12:51 69	25/9/18 21:56 68	27/8/18 3:46 62	28/8/18 4:51 62	29/8/18 5:56 60	30/8/18 23:01 65
25/9/18 12:56 68	25/9/18 22:01 67	27/8/18 3:51 60	28/8/18 4:56 62	29/8/18 6:01 59	30/8/18 23:06 65
25/9/18 13:01 68 25/9/18 13:06 69	25/9/18 22:06 67 25/9/18 22:11 68	27/8/18 3:56 60 27/8/18 4:01 60	28/8/18 5:01 62 28/8/18 5:06 48	29/8/18 6:06 61 29/8/18 6:11 62	30/8/18 23:11 66 30/8/18 23:16 66
25/9/18 13:11 68	25/9/18 22:16 68	27/8/18 4:06 60	28/8/18 5:11 53	29/8/18 6:16 63	30/8/18 23:21 65
25/9/18 13:16 68 25/9/18 13:21 68	25/9/18 22:21 67 25/9/18 22:26 69	27/8/18 4:11 58 27/8/18 4:16 59	28/8/18 5:16 59 28/8/18 5:21 56	29/8/18 6:21 64 29/8/18 6:26 65	30/8/18 23:26 64 30/8/18 23:31 65
25/9/18 13:26 68	25/9/18 22:31 67	27/8/18 4:21 60	28/8/18 5:26 55	29/8/18 6:31 65	30/8/18 23:36 66
25/9/18 13:31 68 25/9/18 13:36 68	25/9/18 22:36 68 25/9/18 22:41 69	27/8/18 4:26 61 27/8/18 4:31 61	28/8/18 5:31 56 28/8/18 5:36 60	29/8/18 6:36 66 29/8/18 6:41 66	30/8/18 23:41 65 30/8/18 23:46 65
25/9/18 13:41 69	25/9/18 22:46 67	27/8/18 4:36 59	28/8/18 5:41 53	29/8/18 6:46 66	30/8/18 23:51 64
25/9/18 13:46 68 25/9/18 13:51 68	25/9/18 22:51 67 25/9/18 22:56 67	27/8/18 4:41 61 27/8/18 4:46 60	28/8/18 5:46 57 28/8/18 5:51 59	29/8/18 6:51 66 29/8/18 6:56 66	30/8/18 23:56 65 31/8/18 0:01 65
25/9/18 13:56 68	26/9/18 19:01 68	27/8/18 4:51 61	28/8/18 5:56 60	29/8/18 23:01 66	31/8/18 0:06 64
25/9/18 14:01 69	26/9/18 19:06 68	27/8/18 4:56 61	28/8/18 6:01 59	29/8/18 23:06 67	31/8/18 0:11 65
25/9/18 14:06 68 25/9/18 14:11 68	26/9/18 19:11 68 26/9/18 19:16 69	27/8/18 5:01 60 27/8/18 5:06 61	28/8/18 6:06 62 28/8/18 6:11 63	29/8/18 23:11 66 29/8/18 23:16 66	31/8/18 0:16 65 31/8/18 0:21 63
25/9/18 14:16 68	26/9/18 19:21 69	27/8/18 5:11 62	28/8/18 6:16 63	29/8/18 23:21 66	31/8/18 0:26 65
25/9/18 14:21 68 25/9/18 14:26 68	26/9/18 19:26 69 26/9/18 19:31 68	27/8/18 5:16 61 27/8/18 5:21 62	28/8/18 6:21 64 28/8/18 6:26 66	29/8/18 23:26 66 29/8/18 23:31 65	31/8/18 0:31 63 31/8/18 0:36 64
25/9/18 14:31 68	26/9/18 19:36 69	27/8/18 5:26 62	28/8/18 6:31 65	29/8/18 23:36 65	31/8/18 0:41 64
25/9/18 14:36 67 25/9/18 14:41 69	26/9/18 19:41 68 26/9/18 19:46 68	27/8/18 5:31 62 27/8/18 5:36 63	28/8/18 6:36 66 28/8/18 6:41 66	29/8/18 23:41 64 29/8/18 23:46 65	31/8/18 0:46 66 31/8/18 0:51 62
25/9/18 14:46 68	26/9/18 19:51 68	27/8/18 5:41 63	28/8/18 6:46 66	29/8/18 23:51 65	31/8/18 0:56 59
25/9/18 14:51 68 25/9/18 14:56 69	26/9/18 19:56 69 26/9/18 20:01 69	27/8/18 5:46 64 27/8/18 5:51 64	28/8/18 6:51 67 28/8/18 6:56 67	29/8/18 23:56 65 30/8/18 0:01 63	31/8/18 1:01 60 31/8/18 1:06 61
25/9/18 15:01 69	26/9/18 20:06 68	27/8/18 5:56 64	28/8/18 23:01 64	30/8/18 0:06 63	31/8/18 1:11 62
25/9/18 15:06 68	26/9/18 20:11 68	27/8/18 6:01 64	28/8/18 23:06 64	30/8/18 0:11 63	31/8/18 1:16 61
25/9/18 15:11 68 25/9/18 15:16 68	26/9/18 20:16 68 26/9/18 20:21 69	27/8/18 6:06 64 27/8/18 6:11 64	28/8/18 23:11 65 28/8/18 23:16 65	30/8/18 0:16 63 30/8/18 0:21 63	31/8/18 1:21 60 31/8/18 1:26 60
25/9/18 15:21 68	26/9/18 20:26 68	27/8/18 6:16 65	28/8/18 23:21 65	30/8/18 0:26 63	31/8/18 1:31 59
25/9/18 15:26 69 25/9/18 15:31 69	26/9/18 20:31 68 26/9/18 20:36 68	27/8/18 6:21 66 27/8/18 6:26 66	28/8/18 23:26 65 28/8/18 23:31 64	30/8/18 0:31 62 30/8/18 0:36 62	31/8/18 1:36 59 31/8/18 1:41 59
25/9/18 15:36 68	26/9/18 20:41 68	27/8/18 6:31 67	28/8/18 23:36 64	30/8/18 0:41 62	31/8/18 1:46 57
25/9/18 15:41 69 25/9/18 15:46 68	26/9/18 20:46 68 26/9/18 20:51 68	27/8/18 6:36 67 27/8/18 6:41 67	28/8/18 23:41 63 28/8/18 23:46 64	30/8/18 0:46 61 30/8/18 0:51 62	31/8/18 1:51 58 31/8/18 1:56 59
25/9/18 15:51 69	26/9/18 20:56 68	27/8/18 6:46 68	28/8/18 23:51 63	30/8/18 0:56 62	31/8/18 2:01 55
25/9/18 15:56 69	26/9/18 21:01 68	27/8/18 6:51 68	28/8/18 23:56 63	30/8/18 1:01 60	31/8/18 2:06 56
25/9/18 16:01 68 25/9/18 16:06 68	26/9/18 21:06 68 26/9/18 21:11 68	27/8/18 6:56 68 27/8/18 23:01 67	29/8/18 0:01 63 29/8/18 0:06 62	30/8/18 1:06 60 30/8/18 1:11 59	31/8/18 2:11 59 31/8/18 2:16 56
25/9/18 16:11 69	26/9/18 21:16 68	27/8/18 23:06 67	29/8/18 0:11 62	30/8/18 1:16 61	31/8/18 2:21 57
25/9/18 16:16 59 25/9/18 16:21 69	26/9/18 21:21 68 26/9/18 21:26 68	27/8/18 23:11 67 27/8/18 23:16 66	29/8/18 0:16 63 29/8/18 0:21 62	30/8/18 1:21 61 30/8/18 1:26 59	31/8/18 2:26 56 31/8/18 2:31 58
25/9/18 16:26 51	26/9/18 21:31 68	27/8/18 23:21 67	29/8/18 0:26 63	30/8/18 1:31 59	31/8/18 2:36 57
25/9/18 16:31 68 25/9/18 16:36 68	26/9/18 21:36 68 26/9/18 21:41 68	27/8/18 23:26 67 27/8/18 23:31 67	29/8/18 0:31 62 29/8/18 0:36 62	30/8/18 1:36 60 30/8/18 1:41 57	31/8/18 2:41 58 31/8/18 2:46 55
25/9/18 16:41 69	26/9/18 21:46 68	27/8/18 23:36 66	29/8/18 0:41 61	30/8/18 1:46 57	31/8/18 2:51 56
25/9/18 16:46 69 25/9/18 16:51 69	26/9/18 21:51 68	27/8/18 23:41 66	29/8/18 0:46 61	30/8/18 1:51 60 20/8/18 1:56 59	31/8/18 2:56 54
25/9/18 16:51 69 25/9/18 16:56 69	26/9/18 21:56 68 26/9/18 22:01 68	27/8/18 23:46 66 27/8/18 23:51 65	29/8/18 0:51 61 29/8/18 0:56 63	30/8/18 1:56 59 30/8/18 2:01 57	31/8/18 3:01 46 31/8/18 3:06 55
25/9/18 17:01 59	26/9/18 22:06 69	27/8/18 23:56 65	29/8/18 1:01 62	30/8/18 2:06 58	31/8/18 3:11 62
25/9/18 17:06 59 25/9/18 17:11 59	26/9/18 22:11 68 26/9/18 22:16 68	28/8/18 0:01 65 28/8/18 0:06 65	29/8/18 1:06 63 29/8/18 1:11 60	30/8/18 2:11 58 30/8/18 2:16 57	31/8/18 3:16 62 31/8/18 3:21 54
25/9/18 17:16 69	26/9/18 22:21 68	28/8/18 0:11 66	29/8/18 1:16 60	30/8/18 2:21 56	31/8/18 3:26 39
25/9/18 17:21 68 25/9/18 17:26 68	26/9/18 22:26 68 26/9/18 22:31 68	28/8/18 0:16 64 28/8/18 0:21 65	29/8/18 1:21 59 29/8/18 1:26 60	30/8/18 2:26 57 30/8/18 2:31 52	31/8/18 3:31 50 31/8/18 3:36 55

1/8/18 3:46	Data 52 52	1/9/18 4:46 6 1/9/18 4:51 6	62 62	ygiene Department 2/9/18 5:51 2/9/18 5:56	64 63	3/9/18 6:56 3/9/18 23:01	67 65	5/9/18 0:01 5/9/18 0:06	64 64	6/9/18 1:06 6/9/18 1:11
1/8/18 3:51 1/8/18 3:56	43 62		62 62	2/9/18 6:01 2/9/18 6:06	63 65	3/9/18 23:06 3/9/18 23:11	65 65	5/9/18 0:11 5/9/18 0:16	63 64	6/9/18 1:16 6/9/18 1:21
1/8/18 4:01	62		62	2/9/18 6:11	63	3/9/18 23:16	66	5/9/18 0:21	67	6/9/18 1:26
1/8/18 4:06	64 39		63 62	2/9/18 6:16 2/9/18 6:21	68 64	3/9/18 23:21	65 65	5/9/18 0:26 5/9/18 0:31	64 63	6/9/18 1:31 6/9/18 1:36
1/8/18 4:11 1/8/18 4:16	39 48		62	2/9/18 6:26	65	3/9/18 23:26 3/9/18 23:31	66	5/9/18 0:36	64	6/9/18 1:41
1/8/18 4:21	55	1/9/18 5:26	63	2/9/18 6:31	65	3/9/18 23:36	66	5/9/18 0:41	63	6/9/18 1:46
1/8/18 4:26 1/8/18 4:31	53 57		63 62	2/9/18 6:36 2/9/18 6:41	65 65	3/9/18 23:41 3/9/18 23:46	65 65	5/9/18 0:46 5/9/18 0:51	63 63	6/9/18 1:51 6/9/18 1:56
1/8/18 4:36	43		63	2/9/18 6:46	66	3/9/18 23:51	65	5/9/18 0:56	62	6/9/18 2:01
1/8/18 4:41	45 56		64 63	2/9/18 6:51 2/9/18 6:56	65 64	3/9/18 23:56 4/9/18 0:01	64	5/9/18 1:01 5/9/18 1:06	62 67	6/9/18 2:06 6/9/18 2:11
1/8/18 4:46 1/8/18 4:51	61		64	2/9/18 23:01	65	4/9/18 0:01	63 64	5/9/18 1:11	62	6/9/18 2:16
1/8/18 4:56	62		63	2/9/18 23:06	65	4/9/18 0:11	65	5/9/18 1:16	61	6/9/18 2:21
1/8/18 5:01 1/8/18 5:06	61 52		64 63	2/9/18 23:11 2/9/18 23:16	65 65	4/9/18 0:16 4/9/18 0:21	64 64	5/9/18 1:21 5/9/18 1:26	61 62	6/9/18 2:26 6/9/18 2:31
1/8/18 5:11	62	1/9/18 6:16	64	2/9/18 23:21	65	4/9/18 0:26	63	5/9/18 1:31	61	6/9/18 2:36
1/8/18 5:16	62 62		66 67	2/9/18 23:26	65 64	4/9/18 0:31	63 65	5/9/18 1:36	62 62	6/9/18 2:41
1/8/18 5:21 1/8/18 5:26	62 56		68	2/9/18 23:31 2/9/18 23:36	64 64	4/9/18 0:36 4/9/18 0:41	65 65	5/9/18 1:41 5/9/18 1:46	62 62	6/9/18 2:46 6/9/18 2:51
1/8/18 5:31	56		67	2/9/18 23:41	65	4/9/18 0:46	63	5/9/18 1:51	61	6/9/18 2:56
1/8/18 5:36 1/8/18 5:41	58 59		67 67	2/9/18 23:46 2/9/18 23:51	65 65	4/9/18 0:51 4/9/18 0:56	63 63	5/9/18 1:56 5/9/18 2:01	61 60	6/9/18 3:01 6/9/18 3:06
1/8/18 5:46	59	1/9/18 6:51 6	67	2/9/18 23:56	68	4/9/18 1:01	63	5/9/18 2:06	60	6/9/18 3:11
1/8/18 5:51 1/8/18 5:56	58 62		67 67	3/9/18 0:01 3/9/18 0:06	64 65	4/9/18 1:06 4/9/18 1:11	63 62	5/9/18 2:11 5/9/18 2:16	61 61	6/9/18 3:16 6/9/18 3:21
1/8/18 6:01	61		67 67	3/9/18 0:08	63	4/9/18 1:16	63	5/9/18 2:21	62	6/9/18 3:26
1/8/18 6:06	63		67	3/9/18 0:16	64	4/9/18 1:21	62	5/9/18 2:26	62	6/9/18 3:31
1/8/18 6:11 1/8/18 6:16	63 63		66 66	3/9/18 0:21 3/9/18 0:26	63 64	4/9/18 1:26 4/9/18 1:31	63 62	5/9/18 2:31 5/9/18 2:36	60 59	6/9/18 3:36 6/9/18 3:41
1/8/18 6:21	63	1/9/18 23:26	67	3/9/18 0:31	62	4/9/18 1:36	63	5/9/18 2:41	59	6/9/18 3:46
1/8/18 6:26	65 65		67 66	3/9/18 0:36	63 64	4/9/18 1:41	62 61	5/9/18 2:46	59 59	6/9/18 3:51
1/8/18 6:31 1/8/18 6:36	65 65		66 66	3/9/18 0:41 3/9/18 0:46	64 63	4/9/18 1:46 4/9/18 1:51	61 62	5/9/18 2:51 5/9/18 2:56	59 59	6/9/18 3:56 6/9/18 4:01
1/8/18 6:41	66	1/9/18 23:46	67	3/9/18 0:51	63	4/9/18 1:56	62	5/9/18 3:01	59	6/9/18 4:06
1/8/18 6:46 1/8/18 6:51	66 66		67 66	3/9/18 0:56 3/9/18 1:01	62 63	4/9/18 2:01 4/9/18 2:06	62 61	5/9/18 3:06 5/9/18 3:11	60 58	6/9/18 4:11 6/9/18 4:16
1/8/18 6:56	67	2/9/18 0:01	66	3/9/18 1:06	63	4/9/18 2:11	61	5/9/18 3:16	60	6/9/18 4:21
1/8/18 23:01 1/8/18 23:06	67 68		65 66	3/9/18 1:11 3/9/18 1:16	62 61	4/9/18 2:16 4/9/18 2:21	61 61	5/9/18 3:21 5/9/18 3:26	59 59	6/9/18 4:26 6/9/18 4:31
1/8/18 23:11	67		66	3/9/18 1:21	63	4/9/18 2:26	60	5/9/18 3:31	60	6/9/18 4:36
1/8/18 23:16	67		66	3/9/18 1:26	62	4/9/18 2:31	61	5/9/18 3:36	59	6/9/18 4:41
1/8/18 23:21 1/8/18 23:26	67 67		66 66	3/9/18 1:31 3/9/18 1:36	62 61	4/9/18 2:36 4/9/18 2:41	60 60	5/9/18 3:41 5/9/18 3:46	60 58	6/9/18 4:46 6/9/18 4:51
1/8/18 23:31	67	2/9/18 0:36	66	3/9/18 1:41	61	4/9/18 2:46	59	5/9/18 3:51	59	6/9/18 4:56
1/8/18 23:36 1/8/18 23:41	67 66		65 65	3/9/18 1:46 3/9/18 1:51	62 61	4/9/18 2:51 4/9/18 2:56	58 59	5/9/18 3:56 5/9/18 4:01	58 60	6/9/18 5:01 6/9/18 5:06
1/8/18 23:46	67		65	3/9/18 1:56	61	4/9/18 3:01	60	5/9/18 4:01	58	6/9/18 5:11
1/8/18 23:51	66		64	3/9/18 2:01	61	4/9/18 3:06	61	5/9/18 4:11	59	6/9/18 5:16
1/8/18 23:56 /9/18 0:01	66 66		64 65	3/9/18 2:06 3/9/18 2:11	60 62	4/9/18 3:11 4/9/18 3:16	60 60	5/9/18 4:16 5/9/18 4:21	59 60	6/9/18 5:21 6/9/18 5:26
/9/18 0:06	66	2/9/18 1:11 6	64	3/9/18 2:16	61	4/9/18 3:21	61	5/9/18 4:26	58	6/9/18 5:31
/9/18 0:11 /9/18 0:16	66 66		65 64	3/9/18 2:21 3/9/18 2:26	61 62	4/9/18 3:26 4/9/18 3:31	59 62	5/9/18 4:31 5/9/18 4:36	58 59	6/9/18 5:36 6/9/18 5:41
/9/18 0:21	66		65	3/9/18 2:31	61	4/9/18 3:36	60	5/9/18 4:41	60	6/9/18 5:46
/9/18 0:26	65 65		64 64	3/9/18 2:36	60 50	4/9/18 3:41 4/9/18 3:46	62	5/9/18 4:46 5/9/18 4:51	60	6/9/18 5:51
/9/18 0:31 /9/18 0:36	65 65		64 64	3/9/18 2:41 3/9/18 2:46	59 64	4/9/18 3:51	60 59	5/9/18 4:56	61 60	6/9/18 5:56 6/9/18 6:01
/9/18 0:41	66		63	3/9/18 2:51	61	4/9/18 3:56	61	5/9/18 5:01	60	6/9/18 6:06
/9/18 0:46 /9/18 0:51	65 65		66 64	3/9/18 2:56 3/9/18 3:01	59 59	4/9/18 4:01 4/9/18 4:06	60 60	5/9/18 5:06 5/9/18 5:11	61 61	6/9/18 6:11 6/9/18 6:16
/9/18 0:56	65	2/9/18 2:01	63	3/9/18 3:06	60	4/9/18 4:11	61	5/9/18 5:16	61	6/9/18 6:21
/9/18 1:01 /9/18 1:06	65 65		63 63	3/9/18 3:11 3/9/18 3:16	59 60	4/9/18 4:16 4/9/18 4:21	60 60	5/9/18 5:21 5/9/18 5:26	62 62	6/9/18 6:26 6/9/18 6:31
/9/18 1:11	65		64	3/9/18 3:21	59	4/9/18 4:26	61	5/9/18 5:31	61	6/9/18 6:36
/9/18 1:16	65 65		64 64	3/9/18 3:26 3/9/18 3:31	59	4/9/18 4:31 4/9/18 4:36	60 60	5/9/18 5:36	62	6/9/18 6:41
/9/18 1:21 /9/18 1:26	65 64		64 64	3/9/18 3:31	61 60	4/9/18 4:36	60 59	5/9/18 5:41 5/9/18 5:46	63 63	6/9/18 6:46 6/9/18 6:51
/9/18 1:31	64	2/9/18 2:36	64	3/9/18 3:41	60	4/9/18 4:46	60	5/9/18 5:51	63	6/9/18 6:56
/9/18 1:36 /9/18 1:41	64 65		64 63	3/9/18 3:46 3/9/18 3:51	61 59	4/9/18 4:51 4/9/18 4:56	61 60	5/9/18 5:56 5/9/18 6:01	63 63	6/9/18 23:01 6/9/18 23:06
/9/18 1:46	65	2/9/18 2:51	64	3/9/18 3:56	59	4/9/18 5:01	60	5/9/18 6:06	63	6/9/18 23:11
/9/18 1:51 /9/18 1:56	64 65		63 64	3/9/18 4:01 3/9/18 4:06	59 59	4/9/18 5:06 4/9/18 5:11	60 60	5/9/18 6:11 5/9/18 6:16	65 66	6/9/18 23:16 6/9/18 23:21
/9/18 1:56 /9/18 2:01	65 64		64 63	3/9/18 4:06 3/9/18 4:11	59 57	4/9/18 5:11 4/9/18 5:16	60 61	5/9/18 6:16 5/9/18 6:21	66 66	6/9/18 23:21
/9/18 2:06	65	2/9/18 3:11 6	63	3/9/18 4:16	60	4/9/18 5:21	61	5/9/18 6:26	66	6/9/18 23:31
/9/18 2:11 /9/18 2:16	65 64		63 63	3/9/18 4:21 3/9/18 4:26	60 59	4/9/18 5:26 4/9/18 5:31	61 62	5/9/18 6:31 5/9/18 6:36	66 67	6/9/18 23:36 6/9/18 23:41
/9/18 2:21	64	2/9/18 3:26	63	3/9/18 4:31	61	4/9/18 5:36	63	5/9/18 6:41	67	6/9/18 23:46
/9/18 2:26 /9/18 2:31	64 64		64 63	3/9/18 4:36 3/9/18 4:41	59 59	4/9/18 5:41 4/9/18 5:46	62 63	5/9/18 6:46 5/9/18 6:51	67 67	6/9/18 23:51 6/9/18 23:56
/9/18 2:31 /9/18 2:36	64 63		63 62	3/9/18 4:41 3/9/18 4:46	59 60	4/9/18 5:46 4/9/18 5:51	63 63	5/9/18 6:51	67 66	7/9/18 0:01
/9/18 2:41	63	2/9/18 3:46	62	3/9/18 4:51	62	4/9/18 5:56	63	5/9/18 23:01	66	7/9/18 0:06
/9/18 2:46 /9/18 2:51	64 64		63 63	3/9/18 4:56 3/9/18 5:01	61 60	4/9/18 6:01 4/9/18 6:06	63 64	5/9/18 23:06 5/9/18 23:11	66 65	7/9/18 0:11 7/9/18 0:16
/9/18 2:56	64	2/9/18 4:01 6	62	3/9/18 5:06	62	4/9/18 6:11	64	5/9/18 23:16	66	7/9/18 0:21
9/18 3:01	63 64		62 85	3/9/18 5:11	61 62	4/9/18 6:16	65 65	5/9/18 23:21	67 65	7/9/18 0:26
/9/18 3:06 /9/18 3:11	64 64		65 62	3/9/18 5:16 3/9/18 5:21	62 62	4/9/18 6:21 4/9/18 6:26	65 66	5/9/18 23:26 5/9/18 23:31	65 65	7/9/18 0:31 7/9/18 0:36
/9/18 3:16	63	2/9/18 4:21 6	62	3/9/18 5:26	61	4/9/18 6:31	66	5/9/18 23:36	65	7/9/18 0:41
/9/18 3:21 /9/18 3:26	63 62		64 62	3/9/18 5:31 3/9/18 5:36	62 62	4/9/18 6:36 4/9/18 6:41	67 67	5/9/18 23:41 5/9/18 23:46	64 65	7/9/18 0:46 7/9/18 0:51
/9/18 3:31	64	2/9/18 4:36	62	3/9/18 5:41	63	4/9/18 6:46	67	5/9/18 23:51	65	7/9/18 0:56
/9/18 3:36 /9/18 3:41	64 63		63 63	3/9/18 5:46 3/9/18 5:51	64 63	4/9/18 6:51 4/9/18 6:56	67 67	5/9/18 23:56 6/9/18 0:01	65 64	7/9/18 1:01 7/9/18 1:06
/9/18 3:41 /9/18 3:46	63 63		63 62	3/9/18 5:51	63 64	4/9/18 6:56 4/9/18 23:01	67 66	6/9/18 0:01	64 64	7/9/18 1:06 7/9/18 1:11
/9/18 3:51	62	2/9/18 4:56	62	3/9/18 6:01	63	4/9/18 23:06	66	6/9/18 0:11	65	7/9/18 1:16
/9/18 3:56 /9/18 4:01	62 62		62 63	3/9/18 6:06 3/9/18 6:11	64 65	4/9/18 23:11 4/9/18 23:16	65 65	6/9/18 0:16 6/9/18 0:21	64 64	7/9/18 1:21 7/9/18 1:26
/9/18 4:06	62	2/9/18 5:11 6	63 63	3/9/18 6:16	66	4/9/18 23:21	65	6/9/18 0:26	65	7/9/18 1:31
/9/18 4:11	61	2/9/18 5:16	64	3/9/18 6:21	66	4/9/18 23:26	65	6/9/18 0:31	65	7/9/18 1:36
/9/18 4:16 /9/18 4:21	62 62		63 63	3/9/18 6:26 3/9/18 6:31	66 67	4/9/18 23:31 4/9/18 23:36	65 65	6/9/18 0:36 6/9/18 0:41	65 64	7/9/18 1:41 7/9/18 1:46
/9/18 4:26	62	2/9/18 5:31	63	3/9/18 6:36	67	4/9/18 23:41	65	6/9/18 0:46	63	7/9/18 1:51
/9/18 4:31	63 62		63 63	3/9/18 6:41 3/9/18 6:46	67 67	4/9/18 23:46 4/9/18 23:51	65 64	6/9/18 0:51 6/9/18 0:56	63 63	7/9/18 1:56 7/9/18 2:01
/9/18 4:36				0/0/10 0:40	07	+/3/10 23:31	64	00:00 01 10 0:00	03	1/3/10/201

7/9/18 2:11 7/9/18 2:16	<u>se Data</u> 61 62	8/9/18 3:16 63 8/9/18 3:21 63	9/9/18 4:21 62 9/9/18 4:26 61	10/9/18 5:26 64 10/9/18 5:31 63	11/9/18 6:31 64 11/9/18 6:36 66	12/9/18 23:36 65 12/9/18 23:41 65
7/9/18 2:21 7/9/18 2:26	61 61	8/9/18 3:26 62 8/9/18 3:31 64	9/9/18 4:31 61 9/9/18 4:36 62	10/9/18 5:36 64 10/9/18 5:41 64	11/9/18 6:41 66 11/9/18 6:46 66	12/9/18 23:46 65 12/9/18 23:51 65
7/9/18 2:31	62	8/9/18 3:36 62	9/9/18 4:41 62	10/9/18 5:46 64	11/9/18 6:51 66	12/9/18 23:56 65
7/9/18 2:36	61	8/9/18 3:41 62	9/9/18 4:46 61	10/9/18 5:51 63	11/9/18 6:56 66	13/9/18 0:01 65
7/9/18 2:41 7/9/18 2:46	60 61	8/9/18 3:46 63 8/9/18 3:51 62	9/9/18 4:51 62 9/9/18 4:56 62	10/9/18 5:56 64 10/9/18 6:01 64	11/9/18 23:01 68 11/9/18 23:06 67	13/9/18 0:06 64 13/9/18 0:11 64
7/9/18 2:51	61	8/9/18 3:56 63	9/9/18 5:01 61	10/9/18 6:06 64	11/9/18 23:11 67	13/9/18 0:16 64
7/9/18 2:56	59	8/9/18 4:01 62	9/9/18 5:06 61	10/9/18 6:11 65	11/9/18 23:16 67	13/9/18 0:21 64
7/9/18 3:01 7/9/18 3:06	61 60	8/9/18 4:06 62 8/9/18 4:11 62	9/9/18 5:11 63 9/9/18 5:16 62	10/9/18 6:16 66 10/9/18 6:21 67	11/9/18 23:21 67 11/9/18 23:26 66	13/9/18 0:26 64 13/9/18 0:31 63
7/9/18 3:11	60	8/9/18 4:16 60	9/9/18 5:21 62	10/9/18 6:26 66	11/9/18 23:31 65	13/9/18 0:36 64
7/9/18 3:16 7/9/18 3:21	60 61	8/9/18 4:21 63 8/9/18 4:26 61	9/9/18 5:26 62 9/9/18 5:31 62	10/9/18 6:31 66 10/9/18 6:36 67	11/9/18 23:36 64 11/9/18 23:41 66	13/9/18 0:41 63 13/9/18 0:46 63
7/9/18 3:26	60	8/9/18 4:31 62	9/9/18 5:36 63	10/9/18 6:41 67	11/9/18 23:46 65	13/9/18 0:51 64
7/9/18 3:31	60	8/9/18 4:36 62	9/9/18 5:41 62	10/9/18 6:46 68	11/9/18 23:51 65	13/9/18 0:56 63
7/9/18 3:36 7/9/18 3:41	60 61	8/9/18 4:41 62 8/9/18 4:46 61	9/9/18 5:46 62 9/9/18 5:51 62	10/9/18 6:51 67 10/9/18 6:56 67	11/9/18 23:56 66 12/9/18 0:01 64	13/9/18 1:01 63 13/9/18 1:06 62
7/9/18 3:46	61	8/9/18 4:51 62	9/9/18 5:56 62	10/9/18 23:01 66	12/9/18 0:06 66	13/9/18 1:11 63
7/9/18 3:51	62	8/9/18 4:56 62	9/9/18 6:01 63	10/9/18 23:06 66	12/9/18 0:11 64	13/9/18 1:16 63
7/9/18 3:56 7/9/18 4:01	60 60	8/9/18 5:01 61 8/9/18 5:06 61	9/9/18 6:06 63 9/9/18 6:11 62	10/9/18 23:11 66 10/9/18 23:16 66	12/9/18 0:16 64 12/9/18 0:21 64	13/9/18 1:21 63 13/9/18 1:26 63
7/9/18 4:06	59	8/9/18 5:11 61	9/9/18 6:16 64	10/9/18 23:21 66	12/9/18 0:26 66	13/9/18 1:31 61
7/9/18 4:11 7/9/18 4:16	58 60	8/9/18 5:16 62 8/9/18 5:21 62	9/9/18 6:21 69 9/9/18 6:26 65	10/9/18 23:26 65 10/9/18 23:31 66	12/9/18 0:31 67 12/9/18 0:36 63	13/9/18 1:36 62 13/9/18 1:41 61
7/9/18 4:21	60	8/9/18 5:26 62	9/9/18 6:31 65	10/9/18 23:36 66	12/9/18 0:41 64	13/9/18 1:46 61
7/9/18 4:26	59	8/9/18 5:31 62	9/9/18 6:36 66	10/9/18 23:41 65	12/9/18 0:46 72	13/9/18 1:51 62
7/9/18 4:31 7/9/18 4:36	60 60	8/9/18 5:36 62 8/9/18 5:41 62	9/9/18 6:41 65 9/9/18 6:46 64	10/9/18 23:46 66 10/9/18 23:51 65	12/9/18 0:51 64 12/9/18 0:56 64	13/9/18 1:56 61 13/9/18 2:01 62
7/9/18 4:41	59	8/9/18 5:46 62	9/9/18 6:51 65	10/9/18 23:56 66	12/9/18 1:01 64	13/9/18 2:06 62
7/9/18 4:46	61	8/9/18 5:51 63	9/9/18 6:56 64	11/9/18 0:01 65	12/9/18 1:06 63	13/9/18 2:11 60
7/9/18 4:51 7/9/18 4:56	61 60	8/9/18 5:56 63 8/9/18 6:01 63	9/9/18 23:01 67 9/9/18 23:06 66	11/9/18 0:06 64 11/9/18 0:11 65	12/9/18 1:11 63 12/9/18 1:16 62	13/9/18 2:16 62 13/9/18 2:21 60
7/9/18 5:01	60	8/9/18 6:06 63	9/9/18 23:11 66	11/9/18 0:16 64	12/9/18 1:21 62	13/9/18 2:26 61
7/9/18 5:06 7/9/18 5:11	60 61	8/9/18 6:11 64 8/9/18 6:16 64	9/9/18 23:16 66 9/9/18 23:21 67	11/9/18 0:21 65 11/9/18 0:26 65	12/9/18 1:26 62 12/9/18 1:31 64	13/9/18 2:31 60 13/9/18 2:36 61
7/9/18 5:16	61	8/9/18 6:21 64	9/9/18 23:26 68	11/9/18 0:31 64	12/9/18 1:36 61	13/9/18 2:41 61
7/9/18 5:21	63	8/9/18 6:26 65	9/9/18 23:31 67	11/9/18 0:36 64	12/9/18 1:41 63	13/9/18 2:46 61
7/9/18 5:26 7/9/18 5:31	61 62	8/9/18 6:31 65 8/9/18 6:36 66	9/9/18 23:36 67 9/9/18 23:41 66	11/9/18 0:41 63 11/9/18 0:46 63	12/9/18 1:46 62 12/9/18 1:51 62	13/9/18 2:51 61 13/9/18 2:56 60
7/9/18 5:36	63	8/9/18 6:41 65	9/9/18 23:46 67	11/9/18 0:51 64	12/9/18 1:56 60	13/9/18 3:01 61
7/9/18 5:41 7/9/18 5:46	62 63	8/9/18 6:46 66 8/9/18 6:51 66	9/9/18 23:51 66 9/9/18 23:56 66	11/9/18 0:56 64 11/9/18 1:01 63	12/9/18 2:01 62 12/9/18 2:06 61	13/9/18 3:06 61 13/9/18 3:11 59
7/9/18 5:51	63	8/9/18 6:56 65	10/9/18 0:01 66	11/9/18 1:06 64	12/9/18 2:11 58	13/9/18 3:16 60
7/9/18 5:56	63	8/9/18 23:01 66	10/9/18 0:06 66	11/9/18 1:11 63	12/9/18 2:16 62	13/9/18 3:21 60
7/9/18 6:01 7/9/18 6:06	64 64	8/9/18 23:06 66 8/9/18 23:11 66	10/9/18 0:11 65 10/9/18 0:16 65	11/9/18 1:16 63 11/9/18 1:21 63	12/9/18 2:21 62 12/9/18 2:26 61	13/9/18 3:26 60 13/9/18 3:31 58
7/9/18 6:11	65	8/9/18 23:16 67	10/9/18 0:21 65	11/9/18 1:26 63	12/9/18 2:31 60	13/9/18 3:36 59
7/9/18 6:16	65 65	8/9/18 23:21 67	10/9/18 0:26 65 10/9/18 0:31 63	11/9/18 1:31 63 11/9/18 1:36 61	12/9/18 2:36 60 12/9/18 2:41 62	13/9/18 3:41 61
7/9/18 6:21 7/9/18 6:26	66	8/9/18 23:26 66 8/9/18 23:31 66	10/9/18 0:31 63 10/9/18 0:36 63	11/9/18 1:36 61 11/9/18 1:41 62	12/9/18 2:46 61	13/9/18 3:46 60 13/9/18 3:51 60
7/9/18 6:31	67	8/9/18 23:36 66	10/9/18 0:41 63	11/9/18 1:46 64	12/9/18 2:51 62	13/9/18 3:56 58
7/9/18 6:36 7/9/18 6:41	67 67	8/9/18 23:41 65 8/9/18 23:46 65	10/9/18 0:46 64 10/9/18 0:51 62	11/9/18 1:51 61 11/9/18 1:56 66	12/9/18 2:56 59 12/9/18 3:01 60	13/9/18 4:01 57 13/9/18 4:06 60
7/9/18 6:46	67	8/9/18 23:51 65	10/9/18 0:56 65	11/9/18 2:01 62	12/9/18 3:06 58	13/9/18 4:11 58
7/9/18 6:51 7/9/18 6:56	67 66	8/9/18 23:56 65 9/9/18 0:01 65	10/9/18 1:01 64 10/9/18 1:06 63	11/9/18 2:06 62 11/9/18 2:11 62	12/9/18 3:11 59 12/9/18 3:16 60	13/9/18 4:16 60 13/9/18 4:21 58
7/9/18 23:01	67	9/9/18 0:06 66	10/9/18 1:11 64	11/9/18 2:16 61	12/9/18 3:21 59	13/9/18 4:26 61
7/9/18 23:06	67	9/9/18 0:11 66	10/9/18 1:16 63	11/9/18 2:21 61	12/9/18 3:26 61	13/9/18 4:31 60
7/9/18 23:11 7/9/18 23:16	66 66	9/9/18 0:16 65 9/9/18 0:21 65	10/9/18 1:21 63 10/9/18 1:26 62	11/9/18 2:26 61 11/9/18 2:31 62	12/9/18 3:31 59 12/9/18 3:36 59	13/9/18 4:36 60 13/9/18 4:41 61
7/9/18 23:21	66	9/9/18 0:26 65	10/9/18 1:31 62	11/9/18 2:36 61	12/9/18 3:41 59	13/9/18 4:46 60
7/9/18 23:26 7/9/18 23:31	66 66	9/9/18 0:31 64 9/9/18 0:36 65	10/9/18 1:36 62 10/9/18 1:41 61	11/9/18 2:41 62 11/9/18 2:46 60	12/9/18 3:46 60 12/9/18 3:51 60	13/9/18 4:51 59 13/9/18 4:56 60
7/9/18 23:36	66	9/9/18 0:41 65	10/9/18 1:46 61	11/9/18 2:51 61	12/9/18 3:56 58	13/9/18 5:01 60
7/9/18 23:41	66	9/9/18 0:46 66	10/9/18 1:51 62	11/9/18 2:56 61	12/9/18 4:01 59	13/9/18 5:06 60
7/9/18 23:46 7/9/18 23:51	66 67	9/9/18 0:51 64 9/9/18 0:56 65	10/9/18 1:56 62 10/9/18 2:01 61	11/9/18 3:01 60 11/9/18 3:06 61	12/9/18 4:06 58 12/9/18 4:11 58	13/9/18 5:11 60 13/9/18 5:16 61
7/9/18 23:56	66	9/9/18 1:01 64	10/9/18 2:06 60	11/9/18 3:11 61	12/9/18 4:16 59	13/9/18 5:21 62
B/9/18 0:01 B/9/18 0:06	65	9/9/18 1:06 64 9/9/18 1:11 65	10/9/18 2:11 60 10/9/18 2:16 61	11/9/18 3:16 61 11/9/18 3:21 59	12/9/18 4:21 59 12/9/18 4:26 59	13/9/18 5:26 62 13/9/18 5:31 62
B/9/18 0:06 B/9/18 0:11	65 65	9/9/18 1:11 65 9/9/18 1:16 64	10/9/18 2:16 61 10/9/18 2:21 62	11/9/18 3:21 59 11/9/18 3:26 52	12/9/18 4:26 59 12/9/18 4:31 58	13/9/18 5:36 61
8/9/18 0:16	67	9/9/18 1:21 64	10/9/18 2:26 60	11/9/18 3:31 54	12/9/18 4:36 60	13/9/18 5:41 61
3/9/18 0:21 3/9/18 0:26	65 65	9/9/18 1:26 64 9/9/18 1:31 64	10/9/18 2:31 60 10/9/18 2:36 61	11/9/18 3:36 53 11/9/18 3:41 61	12/9/18 4:41 59 12/9/18 4:46 59	13/9/18 5:46 62 13/9/18 5:51 63
3/9/18 0:31	65	9/9/18 1:36 65	10/9/18 2:41 60	11/9/18 3:46 61	12/9/18 4:51 60	13/9/18 5:56 62
8/9/18 0:36	66	9/9/18 1:41 64	10/9/18 2:46 61 10/9/18 2:51 61	11/9/18 3:51 61	12/9/18 4:56 59	13/9/18 6:01 63 13/9/18 6:06 64
3/9/18 0:41 3/9/18 0:46	65 65	9/9/18 1:46 63 9/9/18 1:51 63	10/9/18 2:51 61 10/9/18 2:56 59	11/9/18 3:56 60 11/9/18 4:01 61	12/9/18 5:01 59 12/9/18 5:06 60	13/9/18 6:06 64 13/9/18 6:11 65
3/9/18 0:51	65	9/9/18 1:56 63	10/9/18 3:01 59	11/9/18 4:06 50	12/9/18 5:11 60	13/9/18 6:16 64
3/9/18 0:56	66 65	9/9/18 2:01 63 9/9/18 2:06 63	10/9/18 3:06 59 10/9/18 3:11 60	11/9/18 4:11 60 11/9/18 4:16 61	12/9/18 5:16 60 12/9/18 5:21 60	13/9/18 6:21 65 13/9/18 6:26 65
3/9/18 1:01 3/9/18 1:06	65	9/9/18 2:11 63	10/9/18 3:16 60	11/9/18 4:16 61 11/9/18 4:21 61	12/9/18 5:26 62	13/9/18 6:26 65 13/9/18 6:31 66
8/9/18 1:11	64	9/9/18 2:16 62	10/9/18 3:21 61	11/9/18 4:26 46	12/9/18 5:31 61	13/9/18 6:36 66
3/9/18 1:16 3/9/18 1:21	63 65	9/9/18 2:21 63 9/9/18 2:26 63	10/9/18 3:26 60 10/9/18 3:31 60	11/9/18 4:31 51 11/9/18 4:36 62	12/9/18 5:36 61 12/9/18 5:41 62	13/9/18 6:41 67 13/9/18 6:46 67
3/9/18 1:26	64	9/9/18 2:31 63	10/9/18 3:36 59	11/9/18 4:41 62	12/9/18 5:46 62	13/9/18 6:51 67
3/9/18 1:31	63	9/9/18 2:36 63	10/9/18 3:41 61	11/9/18 4:46 61	12/9/18 5:51 63	13/9/18 6:56 67
3/9/18 1:36 3/9/18 1:41	64 64	9/9/18 2:41 63 9/9/18 2:46 62	10/9/18 3:46 61 10/9/18 3:51 60	11/9/18 4:51 60 11/9/18 4:56 55	12/9/18 5:56 63 12/9/18 6:01 62	13/9/18 23:01 67 13/9/18 23:06 67
3/9/18 1:46	63	9/9/18 2:51 63	10/9/18 3:56 58	11/9/18 5:01 61	12/9/18 6:06 63	13/9/18 23:11 66
B/9/18 1:51	64	9/9/18 2:56 63	10/9/18 4:01 61	11/9/18 5:06 62	12/9/18 6:11 64	13/9/18 23:16 66
3/9/18 1:56 3/9/18 2:01	63 64	9/9/18 3:01 62 9/9/18 3:06 62	10/9/18 4:06 58 10/9/18 4:11 61	11/9/18 5:11 62 11/9/18 5:16 62	12/9/18 6:16 64 12/9/18 6:21 65	13/9/18 23:21 66 13/9/18 23:26 65
8/9/18 2:06	63	9/9/18 3:11 63	10/9/18 4:16 61	11/9/18 5:21 62	12/9/18 6:26 66	13/9/18 23:31 66
8/9/18 2:11 8/9/18 2:16	63 63	9/9/18 3:16 63 9/9/18 3:21 63	10/9/18 4:21 59 10/9/18 4:26 61	11/9/18 5:26 58 11/9/18 5:31 55	12/9/18 6:31 66 12/9/18 6:36 67	13/9/18 23:36 67 13/9/18 23:41 65
B/9/18 2:16 B/9/18 2:21	65	9/9/18 3:21 63	10/9/18 4:26 61	11/9/18 5:36 56	12/9/18 6:41 67	13/9/18 23:41 65
8/9/18 2:26	63	9/9/18 3:31 62	10/9/18 4:36 61	11/9/18 5:41 59	12/9/18 6:46 67	13/9/18 23:51 66
8/9/18 2:31 8/9/18 2:36	63 63	9/9/18 3:36 63 9/9/18 3:41 62	10/9/18 4:41 62 10/9/18 4:46 60	11/9/18 5:46 60 11/9/18 5:51 57	12/9/18 6:51 67 12/9/18 6:56 67	13/9/18 23:56 65 14/9/18 0:01 65
3/9/18 2:36 3/9/18 2:41	63	9/9/18 3:41 62 9/9/18 3:46 64	10/9/18 4:46 60	11/9/18 5:56 60	12/9/18 23:01 66	14/9/18 0:01 65
8/9/18 2:46	64	9/9/18 3:51 62	10/9/18 4:56 61	11/9/18 6:01 60	12/9/18 23:06 66	14/9/18 0:11 65
3/9/18 2:51 3/9/18 2:56	63 64	9/9/18 3:56 61 9/9/18 4:01 63	10/9/18 5:01 61 10/9/18 5:06 62	11/9/18 6:06 61 11/9/18 6:11 62	12/9/18 23:11 65 12/9/18 23:16 66	14/9/18 0:16 65 14/9/18 0:21 65
3/9/18 2:56 3/9/18 3:01	62	9/9/18 4:06 61	10/9/18 5:06 62	11/9/18 6:16 63	12/9/18 23:21 66	14/9/18 0:26 65
8/9/18 3:06 8/9/18 3:11	62	9/9/18 4:11 61	10/9/18 5:16 61	11/9/18 6:21 63 11/9/18 6:26 65	12/9/18 23:26 66	14/9/18 0:31 64
	63	9/9/18 4:16 61	10/9/18 5:21 62	LUSUDDZD 05	12/9/18 23:31 65	14/9/18 0:36 64

	Real-time Noise 14/9/18 0:41 14/9/18 0:46	<u>e Data</u> 65 63	RTN1 (Food and Environmental F 15/9/18 1:46 65 15/9/18 1:51 65	16/9/18 2:51 62 16/9/18 2:56 62	17/9/18 3:56 63 17/9/18 4:01 63	18/9/18 5:01 64 18/9/18 5:06 64	19/9/18 6:06 65 19/9/18 6:11 64
		63	15/9/18 2:21 65	16/9/18 3:26 61	17/9/18 4:31 63	18/9/18 5:36 65	19/9/18 6:41 68
		62	15/9/18 2:41 65		17/9/18 4:51 62		19/9/18 23:01 66
	14/9/18 1:56		15/9/18 3:01 65	16/9/18 4:06 62	17/9/18 5:11 62	18/9/18 6:16 66	19/9/18 23:21 65
Advances Construction							19/9/18 23:41 65
Harm Harm <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>							
1447 1447 <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>							
Identification Identif							
Likeling Sch C Likeling Sch S Likeling Sch S <thlikeling sch<="" th=""> S Likeling Sch<td></td><td></td><td></td><td></td><td></td><td></td><td></td></thlikeling>							
Hole Hole <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>							
LASHE 11 01 15978-8-10 62 17978-8-26 65 19978-8238 66 200918-024 64 LASHE 340 02 15978-8-21 04 16978-553 05 19978-8238 66 200918-024 64 LASHE 326 02 15978-8-21 04 16978-553 03 17978-8-41 66 19978-8238 66 200918-024 44 LASHE 326 02 15978-8-21 02 17978-8-41 66 19978-203 66 200918-021 64 200918-021 64 200918-203 67 19978-201 64 200918-11 65 200918-203 67 19978-201 64 200918-12 62 200918-12 63 200918-201 64 200918-12 62 200918-12 63 200918-201 64 200918-12 62 200918-12 63 200918-12 65 200918-11 65 200918-11 65 200918-11 65 200918-11 16 200918-11 16 200918-11							
Harm Harm <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>							
1401 34.6 61 159/14 45 169/14 55 169/14 55 170/14 120/14 67 199/14 199/14 200/14<	14/9/18 3:36		15/9/18 4:41 64	16/9/18 5:46 63	17/9/18 6:51 66		20/9/18 1:01 64
Harding Sch Go Horn Hards							
Hartin Labor 61 15/818 5.00 65 16/818 5.11 64 17/818 22.01 67 18/818 6.24 64 20.918 1.3 64 14/918 4.45 60 15/818 5.21 66 16/918 6.23 67 18/918 0.24 64 20.918 1.3 64 14/918 4.45 61 15/818 5.21 66 16/918 6.21 65 17/918 22.01 67 18/918 0.44 63 20.918 1.3 64 14/918 4.45 61 15/818 5.21 65 16/918 6.21 66 18/918 0.16 63 20.918 1.3 64 19/918 0.16 64 19/918 0.16 63 20.918 2.01 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918 0.16 64 19/918							
1401 640 155/18.51 64 106/18.16 65 177/18/22.21 67 199/18.07.8 64 205/18.13 63 140/18.41 61 155/18.53 65 106/18.23 66 175/18.23 66 199/18.04 64 205/18.13 61 140/18.41 65 105/18.53 65 106/18.23 66 175/18.23 66 199/18.04 64 205/18.15 61 140/18.41 60 155/18.53 65 106/18.64 66 175/18.23 66 199/18.10 62 205/18.25 61 140/18.44 60 155/18.56 65 106/18.65 66 175/18.23 66 199/18.10 62 205/18.25 61 140/18.44 61 155/18.66 155/18.66 166/18.67 166/18.66 199/18.10 63 205/18.26 61 140/18.56 65 106/18.23 65 106/18.23 65 106/18.26 67 109/18.13 63 205/18.26							
Identified 15/81/8 5.16 65 10/81/8 2.21 66 17/81/8 2.22 67 19/81/8 0.21 64 20/81/8 1.44 64 20/81/8 1.44 64 20/81/8 1.44 64 20/81/8 1.44 64 20/81/8 1.44 64 20/81/8 1.44 64 20/81/8 1.44 66 17/81/8 2.24 66 19/81/8 0.44 67							
Hard P4 21 61 150/18 523 65 170/18 23.36 66 190/18 6.41 64 200/18 1.15 62 Hard P4 23 61 150/18 531 65 170/18 23.31 65 190/18 6.55 65 100/18 1.51 65 Hard P4 436 61 150/18 541 65 160/18 6.61 65 170/18 23.51 67 190/18 1.05 62 200/18 1.51 66 190/18 1.05 62 200/18 2.05 61 140/18 4.44 61 150/18 5.05 61 150/18 5.05 61 150/18 5.05 61 150/18 5.05 61 150/18 5.05 62 150/18 5.05 62 150/18 5.05 62 150/18 5.05 62 150/18 5.05 62 150/18 5.05 63 150/18 5.05 63 150/18 5.01 66 150/18 5.01 60 150/18 5.01 60 150/18 5.01 60 150/18 5.01 60 150/18 5.01 60 150/18 5.01 60 150/18 5.01 60 150/18 5.01 60 150/18 5.01 60 150/18 5.01 <t< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>							
Hard Haze ei Hstell BS36 Eisell BS366 Eisell BS366 Ei							
HA191431 60 150/16536 65 160/16641 65 173/182346 66 190/1656 63 200/18211 61 HA1914466 61 150/16556 65 160/16650 66 190/16105 66 190/16116 62 200/18211 61 HA1914466 61 150/16556 65 160/16201 66 190/16116 63 200/18211 61 HA1914456 61 150/16506 66 160/162206 62 180/16011 66 190/161116 63 200/182216 61 HA1916511 61 150/16616 66 160/162226 63 180/16026 67 190/16131 63 200/18246 61 140/18256 62 180/16026 65 190/16131 63 200/18246 61 140/18256 63 190/16131 63 200/18246 61 140/18256 63 190/16131 63 200/18267 61 200/18267 61 200/18267 61 200/18267							
14Ard 14.44 60 15b/16.55 65 17b/16.23.56 66 19b/16.10 62 200/18.20 61 14Ard 14.46 61 15b/16.55 65 16b/16.55 65 18b/16.01 66 19b/16.10 62 200/18.21 61 14Ard 14.46 61 15b/16.60 65 16b/16.21 62 18b/16.01 66 19b/16.11 63 200/18.22 61 14Ard 15.51 61 15b/16.60 65 16b/18.22 62 18b/16.02 66 19b/16.12 63 200/18.22 62 200/18.22 62 200/18.22 62 200/18.22 62 200/18.22 62 200/18.22 62 200/18.22 62 200/18.22 62 200/18.23 63 150/16.01 65 190/16.11 65 190/16.11 64 62 200/18.23 63 190/16.11 65 190/16.15 61 200/18.23 63 190/16.15 61 200/18.23 63 140/17.15 65 190/16.2							
Idania Idania<							
Harman Harman<				16/9/18 23:01 62			20/9/18 2:16 61
14/4785.05 61 15/916.011 65 15/916.021 63 19/917.126 62 200/11223 61 14/9185.15 60 15/916.21 66 16/918.232 62 18/918.031 65 19/917.126 62 200/11223 61 14/9185.31 62 15/916.63 68 16/918.234 62 19/918.14 65 19/918.151 61 200/11225 61 14/9185.36 62 15/916.63 68 16/918.234 62 19/918.166 61 200/11225 61 14/9185.56 62 15/916.64 67 19/918.156 61 200/1123 61 15/918.236 61 19/918.206 61 200/1133 61 14/9185.56 64 15/918.201 66 17/918.016 62 18/918.116 66 19/918.226 61 200/1133.01 61 14/918.656 64 15/918.201 66 17/918.016 62 18/918.121 65 19/918.226 61 200/113.306 61 14/918.656 64 15/918.2031 66							
Hám Strill 6:1 15/018.61:6 66 15/018.22:6 62 18/018.02:8 65 19/018.13 63 200/112.34 60 14/018.51:8 61 15/018.62:8 66 19/018.13 63 200/112.34 61 14/018.52:1 61 15/018.63 65 19/018.14 62 200/112.34 61 14/018.53:0 62 15/018.64 68 16/018.23.4 62 19/018.04 65 19/018.15.6 61 200/112.36 61 14/018.53:0 62 15/018.64 68 16/018.23.5 63 19/018.05 64 19/018.01 61 200/113.30 61 14/018.54.6 63 15/018.23.01 66 17/018.01 61 19/018.11 64 19/018.21 65 19/018.21 62 200/113.33 61 14/018.65.6 64 15/018.23.1 66 17/018.01 61 19/018.12 65 19/018.22.1 61 200/113.33 61 200/113.33 61 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$	14/9/18 5:11	61	15/9/18 6:16 66	16/9/18 23:21 62	18/9/18 0:26 67	19/9/18 1:31 63	20/9/18 2:36 60
144978 8.26 63 15978 6.21 68 16978 2.33 63 19978 0.41 65 19978 11.46 62 209718 2.56 61 144978 8.36 62 15978 8.36 62 15978 8.36 63 199718 0.56 64 199718 1.56 61 209718 2.56 61 144978 8.34 62 15978 8.36 66 179718 0.01 62 199718 1.16 64 199718 2.11 62 209718 3.25 60 144978 8.61 63 15978 8.26 66 179718 0.01 62 199718 1.16 64 199718 2.27 61 209718 3.27 60 144978 8.61 64 15978 8.23 66 179718 0.21 62 189718 1.21 64 199718 2.24 61 209718 3.35 63 149718 6.24 199718 2.24 61 209718 3.35 65 179718 0.24 61 199718 2.24 61 209718 3.35 65 179718 0.25 61 199718 2.24 61 209718 3.35 65 179718 0.26 61 199718 2.24 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>							
14498 8541 62 159/18 646 67 169/18 2351 63 169/18 101 65 199/18 206 61 209/18 316 61 149/18 851 63 159/18 656 68 179/18 0.01 62 139/18 106 65 199/18 2.16 61 209/18 316 61 149/18 855 64 159/18 2.211 66 179/18 0.01 62 139/18 1.06 65 199/18 2.16 61 209/18 3.31 61 149/18 8.06 64 159/18 2.211 66 179/18 0.16 62 139/18 1.26 64 199/18 2.26 61 209/18 3.36 60 149/18 6.16 65 159/18 2.32.1 66 179/18 0.26 62 139/18 1.36 64 199/18 2.31 61 209/18 3.46 60 149/18 8.26 66 159/18 2.32.3 66 179/18 0.36 61 139/18 1.36 64 199/18 2.46 61 209/18 3.46 60 209/18 3.46 60 209/18 3.46 60 209/18 4.46 61 209/18 4.46 61 209/18 4.46 61 209/18 4.46 61 209/18 4.46 61		62	15/9/18 6:36 68	16/9/18 23:41 62	18/9/18 0:46 65	19/9/18 1:51 61	20/9/18 2:56 61
14/9/18.5/56 64 15/9/18.23:00 66 17/9/18.01:16 64 19/9/18.21:6 61 20/9/18.32:6 61 14/9/18.61/6 63 15/9/18.23:11 66 17/9/18.01:6 62 19/9/18.11:6 64 19/9/18.22:1 61 20/9/18.32:6 61 14/9/18.61/6 66 15/9/18.23:1 66 17/9/18.01:6 62 19/9/18.12:6 64 19/9/18.24:6 61 20/9/18.34 61 14/9/18.61/6 66 15/9/18.23:1 66 17/9/18.02:6 62 19/9/18.14 65 19/9/18.24:6 61 20/9/18.34 66 20/9/18.34 66 19/9/18.24:6 62 20/9/18.34 66 20/9/18.34 66 19/9/18.24:6 63 19/9/18.24:6 62 20/9/18.26 62 20/9/18.26 62 20/9/18.26 62 20/9/18.26 62 20/9/18.26 60 20/9/18.26 60 20/9/18.26 60 20/9/18.26 60 20/9/18.26 60 20/9/18.26 60 20/9/18.26 60 20/9/18.26 60 20/9/18.26 61 20/9/18.26 61 20/9/18.26							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$						19/9/18 2:26 61	
14/9/18 6.21 66 15/9/18 2.32 65 17/9/18 0.31 61 18/9/18 1:36 64 19/9/18 2.41 61 20/9/18 3:51 59 14/9/18 6:31 66 15/9/18 2:33 66 17/9/18 0:36 61 18/9/18 1:46 64 19/9/18 2:56 62 20/9/18 3:56 62 14/9/18 6:36 67 15/9/18 2:34 66 17/9/18 0:46 61 18/9/18 1:56 64 19/9/18 2:56 60 20/9/18 4:06 60 14/9/18 6:56 67 15/9/18 2:356 65 17/9/18 0:56 61 18/9/18 2:06 63 19/9/18 3:11 61 20/9/18 4:16 61 14/9/18 6:56 66 15/9/18 2:356 65 17/9/18 1:06 67 18/9/18 2:16 64 19/9/18 3:16 61 20/9/18 4:16 61 14/9/18 2:301 67 16/9/18 0:01 65 17/9/18 1:16 61 18/9/18 2:26 62 19/9/18 3:31 60 20/9/18 4:31 61 20/9/18 4:31 61 20/9/18 4:36 62 19/9/18 3:31 60 20/9/18 4:36 63 19/9/18 3:31 60 20/9/18 4:36 63<							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
14/9/18 6.36 67 15/9/18 23:41 66 17/9/18 0:46 61 18/9/18 1:51 65 19/9/18 2:56 60 20/9/18 4:01 59 14/9/18 6:46 67 15/9/18 23:51 65 17/9/18 0:56 61 18/9/18 2:01 62 19/9/18 3:01 61 20/9/18 4:11 59 14/9/18 6:56 66 16/9/18 0:01 65 17/9/18 1:06 67 18/9/18 2:01 62 19/9/18 3:01 61 20/9/18 4:21 60 14/9/18 2:06 67 16/9/18 0:06 65 17/9/18 1:16 61 18/9/18 2:21 67 19/9/18 3:24 60 20/9/18 4:21 60 14/9/18 2:31 63 16/9/18 0:01 65 17/9/18 1:26 61 18/9/18 2:21 67 19/9/18 3:34 61 20/9/14 4:44 60 14/9/18 2:31 63 16/9/18 0:21 65 17/9/18 1:26 61 18/9/18 2:21 63 19/9/18 3:34 61 20/9/14 4:44 60 14/9/18 2:32 66 16/9/18 0:26 65 17/9/18 1:26 61 18/9/18 2:21 63 19/9/18 3:44 61 20/9/18 4:51<							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$	14/9/18 23:26	68	16/9/18 0:31 65	17/9/18 1:36 61	18/9/18 2:41 63	19/9/18 3:46 58	20/9/18 4:51 60
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$							
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	14/9/18 23:46	67	16/9/18 0:51 64	17/9/18 1:56 62	18/9/18 3:01 64	19/9/18 4:06 61	20/9/18 5:11 61
$\begin{array}{cccccccccccccccccccccccccccccccccccc$							
$\begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$	15/9/18 0:06	67	16/9/18 1:11 63	17/9/18 2:16 61	18/9/18 3:21 63	19/9/18 4:26 61	20/9/18 5:31 62
$\begin{array}{cccccccccccccccccccccccccccccccccccc$							
$\begin{array}{cccccccccccccccccccccccccccccccccccc$							
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$	15/9/18 0:26	66	16/9/18 1:31 63	17/9/18 2:36 61	18/9/18 3:41 64	19/9/18 4:46 59	20/9/18 5:51 63
$\begin{array}{cccccccccccccccccccccccccccccccccccc$							
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	15/9/18 0:41	66	16/9/18 1:46 63	17/9/18 2:51 61	18/9/18 3:56 63	19/9/18 5:01 61	20/9/18 6:06 64
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	15/9/18 0:46	66	16/9/18 1:51 63	17/9/18 2:56 61	18/9/18 4:01 63	19/9/18 5:06 60	20/9/18 6:11 64
$\begin{array}{cccccccccccccccccccccccccccccccccccc$							
15/9/18 1:06 66 16/9/18 2:11 62 17/9/18 3:16 61 18/9/18 4:21 63 19/9/18 5:26 62 20/9/18 6:31 66 15/9/18 1:11 66 16/9/18 2:16 62 17/9/18 3:21 61 18/9/18 4:26 64 19/9/18 5:31 62 20/9/18 6:31 66 15/9/18 1:16 66 16/9/18 2:16 63 17/9/18 3:26 62 18/9/18 4:31 64 19/9/18 5:31 62 20/9/18 6:41 67 15/9/18 1:21 65 16/9/18 2:26 62 17/9/18 3:31 62 18/9/18 4:36 63 19/9/18 5:41 61 20/9/18 6:41 67 15/9/18 1:26 66 16/9/18 2:31 63 17/9/18 3:36 63 18/9/18 4:41 64 19/9/18 5:41 61 20/9/18 6:51 67 15/9/18 1:36 67 16/9/18 2:41 61 17/9/18 3:41 63 18/9/18 4:45 63 19/9/18 5:51 63 20/9/18 6:51 67 15/9/18 1:36 67 16/9/18 2:41 61 17/9/18 3		66	16/9/18 2:06 62	17/9/18 3:11 61	18/9/18 4:16 64	19/9/18 5:21 62	20/9/18 6:26 66
15/9/18 1:16 66 16/9/18 2:21 63 17/9/18 3:26 62 18/9/18 4:31 64 19/9/18 5:36 63 20/9/18 6:41 67 15/9/18 1:21 65 16/9/18 2:26 62 17/9/18 3:31 62 18/9/18 4:36 63 19/9/18 5:36 63 20/9/18 6:41 67 15/9/18 1:26 66 16/9/18 2:36 63 17/9/18 3:31 62 18/9/18 4:36 63 19/9/18 5:46 61 20/9/18 6:46 68 15/9/18 1:31 66 16/9/18 2:36 63 17/9/18 3:41 63 18/9/18 4:41 64 19/9/18 5:46 61 20/9/18 6:56 65 15/9/18 1:36 67 16/9/18 2:41 61 17/9/18 3:41 63 18/9/18 4:51 63 19/9/18 5:56 63 20/9/18 6:56 65 15/9/18 1:36 67 16/9/18 2:41 61 17/9/18 3:46 64 18/9/18 4:51 63 19/9/18 5:56 63 20/9/18 2:301 66							
15/9/18 1:21 65 16/9/18 2:26 62 17/9/18 3:31 62 18/9/18 4:36 63 19/9/18 5:41 61 20/9/18 6:46 68 15/9/18 1:26 66 16/9/18 2:31 63 18/9/18 4:41 64 19/9/18 5:46 61 20/9/18 6:51 67 15/9/18 1:31 66 16/9/18 2:36 63 18/9/18 4:41 64 19/9/18 5:51 63 20/9/18 65 65 15/9/18 1:31 66 16/9/18 2:41 61 17/9/18 3:46 64 18/9/18 4:55 63 20/9/18 65 50 15/9/18 1:36 67 16/9/18 2:41 61 17/9/18 3:46 64 18/9/18 4:55 63 20/9/18 20/9/18 65							
15/9/18 1:31 66 16/9/18 2:36 63 17/9/18 3:41 63 18/9/18 4:46 63 19/9/18 5:51 63 20/9/18 6:56 65 15/9/18 1:36 67 16/9/18 2:41 61 17/9/18 3:46 64 18/9/18 4:51 63 19/9/18 5:56 63 20/9/18 23:01 66	15/9/18 1:21	65	16/9/18 2:26 62	17/9/18 3:31 62	18/9/18 4:36 63	19/9/18 5:41 61	20/9/18 6:46 68
15/9/18 1:36 67 16/9/18 2:41 61 17/9/18 3:46 64 18/9/18 4:51 63 19/9/18 5:56 63 20/9/18 23:01 66							

Real-time Noise Data	RTN1 (Food and Environmental				
20/9/18 23:11 66	22/9/18 0:16 65	23/9/18 1:21 63	24/9/18 2:26 60	25/9/18 3:31 64	26/9/18 4:36 62
20/9/18 23:16 66 20/9/18 23:21 65	22/9/18 0:21 66 22/9/18 0:26 66	23/9/18 1:26 63 23/9/18 1:31 64	24/9/18 2:31 60 24/9/18 2:36 60	25/9/18 3:36 63 25/9/18 3:41 63	26/9/18 4:41 61 26/9/18 4:46 60
20/9/18 23:26 66	22/9/18 0:31 66	23/9/18 1:36 63	24/9/18 2:41 60	25/9/18 3:46 62	26/9/18 4:51 61
20/9/18 23:31 65 20/9/18 23:36 66	22/9/18 0:36 65 22/9/18 0:41 64	23/9/18 1:41 63 23/9/18 1:46 64	24/9/18 2:46 59 24/9/18 2:51 60	25/9/18 3:51 63 25/9/18 3:56 63	26/9/18 4:56 61 26/9/18 5:01 61
20/9/18 23:41 65	22/9/18 0:46 65 22/9/18 0:51 65	23/9/18 1:51 63	24/9/18 2:56 67 24/9/18 3:01 58	25/9/18 4:01 63	26/9/18 5:06 61
20/9/18 23:46 65 20/9/18 23:51 66	22/9/18 0:51 65 22/9/18 0:56 65	23/9/18 1:56 63 23/9/18 2:01 62	24/9/18 3:01 58 24/9/18 3:06 59	25/9/18 4:06 63 25/9/18 4:11 62	26/9/18 5:11 61 26/9/18 5:16 61
20/9/18 23:56 65 21/9/18 0:01 65	22/9/18 1:01 65 22/9/18 1:06 64	23/9/18 2:06 63 23/9/18 2:11 65	24/9/18 3:11 59 24/9/18 3:16 58	25/9/18 4:16 62 25/9/18 4:21 62	26/9/18 5:21 61 26/9/18 5:26 62
21/9/18 0:06 65	22/9/18 1:11 65	23/9/18 2:16 64	24/9/18 3:21 59	25/9/18 4:26 63	26/9/18 5:31 63
21/9/18 0:11 65 21/9/18 0:16 65	22/9/18 1:16 64 22/9/18 1:21 64	23/9/18 2:21 63 23/9/18 2:26 63	24/9/18 3:26 59 24/9/18 3:31 60	25/9/18 4:31 64 25/9/18 4:36 64	26/9/18 5:36 63 26/9/18 5:41 63
21/9/18 0:21 65	22/9/18 1:26 64	23/9/18 2:31 63	24/9/18 3:36 59	25/9/18 4:41 63	26/9/18 5:46 64
21/9/18 0:26 64 21/9/18 0:31 64	22/9/18 1:31 64 22/9/18 1:36 64	23/9/18 2:36 63 23/9/18 2:41 63	24/9/18 3:41 61 24/9/18 3:46 59	25/9/18 4:46 63 25/9/18 4:51 63	26/9/18 5:51 64 26/9/18 5:56 64
21/9/18 0:36 64	22/9/18 1:41 64	23/9/18 2:46 62	24/9/18 3:51 59	25/9/18 4:56 64	26/9/18 6:01 64
21/9/18 0:41 64 21/9/18 0:46 64	22/9/18 1:46 63 22/9/18 1:51 64	23/9/18 2:51 63 23/9/18 2:56 62	24/9/18 3:56 59 24/9/18 4:01 60	25/9/18 5:01 63 25/9/18 5:06 63	26/9/18 6:06 64 26/9/18 6:11 65
21/9/18 0:51 64	22/9/18 1:56 64	23/9/18 3:01 63	24/9/18 4:06 57	25/9/18 5:11 63	26/9/18 6:16 66
21/9/18 0:56 64 21/9/18 1:01 63	22/9/18 2:01 64 22/9/18 2:06 63	23/9/18 3:06 63 23/9/18 3:11 62	24/9/18 4:11 61 24/9/18 4:16 59	25/9/18 5:16 63 25/9/18 5:21 63	26/9/18 6:21 66 26/9/18 6:26 66
21/9/18 1:06 63 21/9/18 1:11 64	22/9/18 2:11 63 22/9/18 2:16 64	23/9/18 3:16 63 23/9/18 3:21 62	24/9/18 4:21 59 24/9/18 4:26 58	25/9/18 5:26 63 25/9/18 5:31 64	26/9/18 6:31 66 26/9/18 6:36 67
21/9/18 1:16 63	22/9/18 2:21 64	23/9/18 3:26 63	24/9/18 4:31 60	25/9/18 5:36 63	26/9/18 6:41 68
21/9/18 1:21 62 21/9/18 1:26 63	22/9/18 2:26 64 22/9/18 2:31 64	23/9/18 3:31 63 23/9/18 3:36 62	24/9/18 4:36 60 24/9/18 4:41 61	25/9/18 5:41 63 25/9/18 5:46 63	26/9/18 6:46 68 26/9/18 6:51 68
21/9/18 1:31 62	22/9/18 2:36 63	23/9/18 3:41 62	24/9/18 4:46 58	25/9/18 5:51 65	26/9/18 6:56 68
21/9/18 1:36 62 21/9/18 1:41 61	22/9/18 2:41 63 22/9/18 2:46 64	23/9/18 3:46 63 23/9/18 3:51 62	24/9/18 4:51 60 24/9/18 4:56 60	25/9/18 5:56 63 25/9/18 6:01 64	26/9/18 23:01 66 26/9/18 23:06 66
21/9/18 1:46 61	22/9/18 2:51 63	23/9/18 3:56 62	24/9/18 5:01 60	25/9/18 6:06 64	26/9/18 23:11 66
21/9/18 1:51 62 21/9/18 1:56 61	22/9/18 2:56 63 22/9/18 3:01 63	23/9/18 4:01 61 23/9/18 4:06 61	24/9/18 5:06 61 24/9/18 5:11 61	25/9/18 6:11 65 25/9/18 6:16 65	26/9/18 23:16 67 26/9/18 23:21 66
21/9/18 2:01 61	22/9/18 3:06 63	23/9/18 4:11 61	24/9/18 5:16 61	25/9/18 6:21 65	26/9/18 23:26 66
21/9/18 2:06 62 21/9/18 2:11 62	22/9/18 3:11 63 22/9/18 3:16 63	23/9/18 4:16 61 23/9/18 4:21 62	24/9/18 5:21 62 24/9/18 5:26 62	25/9/18 6:26 66 25/9/18 6:31 66	26/9/18 23:31 66 26/9/18 23:36 66
21/9/18 2:16 60	22/9/18 3:21 63	23/9/18 4:26 61	24/9/18 5:31 62	25/9/18 6:36 67	26/9/18 23:41 65
21/9/18 2:21 61 21/9/18 2:26 61	22/9/18 3:26 63 22/9/18 3:31 62	23/9/18 4:31 62 23/9/18 4:36 62	24/9/18 5:36 63 24/9/18 5:41 63	25/9/18 6:41 66 25/9/18 6:46 66	26/9/18 23:46 65 26/9/18 23:51 66
21/9/18 2:31 61	22/9/18 3:36 62	23/9/18 4:41 62	24/9/18 5:46 62	25/9/18 6:51 66	26/9/18 23:56 65
21/9/18 2:36 61 21/9/18 2:41 62	22/9/18 3:41 62 22/9/18 3:46 63	23/9/18 4:46 62 23/9/18 4:51 62	24/9/18 5:51 62 24/9/18 5:56 63	25/9/18 6:56 66 25/9/18 23:01 65	
21/9/18 2:46 60	22/9/18 3:51 63	23/9/18 4:56 60	24/9/18 6:01 63	25/9/18 23:06 65	
21/9/18 2:51 61 21/9/18 2:56 61	22/9/18 3:56 63 22/9/18 4:01 63	23/9/18 5:01 62 23/9/18 5:06 61	24/9/18 6:06 63 24/9/18 6:11 63	25/9/18 23:11 65 25/9/18 23:16 64	
21/9/18 3:01 62	22/9/18 4:06 62	23/9/18 5:11 62	24/9/18 6:16 65	25/9/18 23:21 65	
21/9/18 3:06 62 21/9/18 3:11 61	22/9/18 4:11 62 22/9/18 4:16 61	23/9/18 5:16 62 23/9/18 5:21 62	24/9/18 6:21 65 24/9/18 6:26 65	25/9/18 23:26 65 25/9/18 23:31 66	
21/9/18 3:16 61	22/9/18 4:21 62	23/9/18 5:26 62	24/9/18 6:31 66	25/9/18 23:36 65	
21/9/18 3:21 60 21/9/18 3:26 61	22/9/18 4:26 62 22/9/18 4:31 61	23/9/18 5:31 62 23/9/18 5:36 62	24/9/18 6:36 66 24/9/18 6:41 67	25/9/18 23:41 65 25/9/18 23:46 65	
21/9/18 3:31 61	22/9/18 4:36 63	23/9/18 5:41 62	24/9/18 6:46 66	25/9/18 23:51 65	
21/9/18 3:36 62 21/9/18 3:41 60	22/9/18 4:41 61 22/9/18 4:46 63	23/9/18 5:46 63 23/9/18 5:51 63	24/9/18 6:51 67 24/9/18 6:56 67	25/9/18 23:56 64 26/9/18 0:01 64	
21/9/18 3:46 61	22/9/18 4:51 62	23/9/18 5:56 62	24/9/18 23:01 68	26/9/18 0:06 64	
21/9/18 3:51 59 21/9/18 3:56 60	22/9/18 4:56 62 22/9/18 5:01 62	23/9/18 6:01 63 23/9/18 6:06 62	24/9/18 23:06 67 24/9/18 23:11 67	26/9/18 0:11 63 26/9/18 0:16 64	
21/9/18 4:01 61	22/9/18 5:06 62	23/9/18 6:11 63	24/9/18 23:16 67	26/9/18 0:21 64	
21/9/18 4:06 60 21/9/18 4:11 60	22/9/18 5:11 60 22/9/18 5:16 62	23/9/18 6:16 63 23/9/18 6:21 65	24/9/18 23:21 67 24/9/18 23:26 67	26/9/18 0:26 63 26/9/18 0:31 64	
21/9/18 4:16 61 21/9/18 4:21 60	22/9/18 5:21 63 22/9/18 5:26 63	23/9/18 6:26 65 23/9/18 6:31 65	24/9/18 23:31 66 24/9/18 23:36 68	26/9/18 0:36 62 26/9/18 0:41 63	
21/9/18 4:26 62	22/9/18 5:31 63	23/9/18 6:36 65	24/9/18 23:41 68	26/9/18 0:46 63	
21/9/18 4:31 60 21/9/18 4:36 61	22/9/18 5:36 63 22/9/18 5:41 64	23/9/18 6:41 65 23/9/18 6:46 65	24/9/18 23:46 68 24/9/18 23:51 67	26/9/18 0:51 62 26/9/18 0:56 62	
21/9/18 4:41 60	22/9/18 5:46 64	23/9/18 6:51 65	24/9/18 23:56 67	26/9/18 1:01 63	
21/9/18 4:46 61 21/9/18 4:51 61	22/9/18 5:51 64 22/9/18 5:56 64	23/9/18 6:56 65 23/9/18 23:01 66	25/9/18 0:01 67 25/9/18 0:06 67	26/9/18 1:06 62 26/9/18 1:11 63	
21/9/18 4:56 61	22/9/18 6:01 63	23/9/18 23:06 65	25/9/18 0:11 66	26/9/18 1:16 63	
21/9/18 5:01 60 21/9/18 5:06 62	22/9/18 6:06 64 22/9/18 6:11 65	23/9/18 23:11 66 23/9/18 23:16 65	25/9/18 0:16 66 25/9/18 0:21 66	26/9/18 1:21 62 26/9/18 1:26 63	
21/9/18 5:11 61	22/9/18 6:16 65	23/9/18 23:21 65	25/9/18 0:26 66	26/9/18 1:31 61	
21/9/18 5:16 61 21/9/18 5:21 61	22/9/18 6:21 65 22/9/18 6:26 65	23/9/18 23:26 65 23/9/18 23:31 65	25/9/18 0:31 66 25/9/18 0:36 66	26/9/18 1:36 63 26/9/18 1:41 63	
21/9/18 5:26 62	22/9/18 6:31 66	23/9/18 23:36 64	25/9/18 0:41 69	26/9/18 1:46 62	
21/9/18 5:31 63 21/9/18 5:36 63	22/9/18 6:36 66 22/9/18 6:41 66	23/9/18 23:41 65 23/9/18 23:46 64	25/9/18 0:46 73 25/9/18 0:51 72	26/9/18 1:51 60 26/9/18 1:56 61	
21/9/18 5:41 62	22/9/18 6:46 67	23/9/18 23:51 64	25/9/18 0:56 70	26/9/18 2:01 61	
21/9/18 5:51 64	22/9/18 6:51 66 22/9/18 6:56 67	24/9/18 0:01 64	25/9/18 1:06 66	26/9/18 2:06 62 26/9/18 2:11 61	
21/9/18 5:56 63 21/9/18 6:01 64	22/9/18 23:01 66 22/9/18 23:06 65	24/9/18 0:06 64 24/9/18 0:11 64	25/9/18 1:11 66 25/9/18 1:16 66	26/9/18 2:16 60 26/9/18 2:21 61	
21/9/18 6:06 64	22/9/18 23:11 65	24/9/18 0:16 63	25/9/18 1:21 66	26/9/18 2:26 61	
21/9/18 6:11 64 21/9/18 6:16 66	22/9/18 23:16 66 22/9/18 23:21 66	24/9/18 0:21 64 24/9/18 0:26 63	25/9/18 1:26 65 25/9/18 1:31 65	26/9/18 2:31 61 26/9/18 2:36 61	
21/9/18 6:21 65	22/9/18 23:26 66	24/9/18 0:31 65	25/9/18 1:36 66	26/9/18 2:41 61	
21/9/18 6:26 66 21/9/18 6:31 66	22/9/18 23:31 66 22/9/18 23:36 66	24/9/18 0:36 64 24/9/18 0:41 61	25/9/18 1:41 67 25/9/18 1:46 66	26/9/18 2:46 61 26/9/18 2:51 61	
21/9/18 6:36 67	22/9/18 23:41 66	24/9/18 0:46 62	25/9/18 1:51 65	26/9/18 2:56 59	
21/9/18 6:41 67 21/9/18 6:46 67	22/9/18 23:46 65 22/9/18 23:51 65	24/9/18 0:51 62 24/9/18 0:56 62	25/9/18 1:56 64 25/9/18 2:01 66	26/9/18 3:01 59 26/9/18 3:06 59	
21/9/18 6:51 66	22/9/18 23:56 66	24/9/18 1:01 64	25/9/18 2:06 66	26/9/18 3:11 59	
21/9/18 6:56 66 21/9/18 23:01 66	23/9/18 0:01 65 23/9/18 0:06 65	24/9/18 1:06 62 24/9/18 1:11 62	25/9/18 2:11 68 25/9/18 2:16 68	26/9/18 3:16 60 26/9/18 3:21 59	
21/9/18 23:06 66	23/9/18 0:11 65	24/9/18 1:16 62	25/9/18 2:21 66	26/9/18 3:26 60	
21/9/18 23:11 67 21/9/18 23:16 66	23/9/18 0:16 66 23/9/18 0:21 65	24/9/18 1:21 62 24/9/18 1:26 64	25/9/18 2:26 65 25/9/18 2:31 69	26/9/18 3:31 60 26/9/18 3:36 61	
21/9/18 23:21 66	23/9/18 0:26 66	24/9/18 1:31 61	25/9/18 2:36 68	26/9/18 3:41 62	
21/9/18 23:26 66 21/9/18 23:31 66	23/9/18 0:31 65 23/9/18 0:36 65	24/9/18 1:36 61 24/9/18 1:41 61	25/9/18 2:41 67 25/9/18 2:46 64	26/9/18 3:46 59 26/9/18 3:51 60	
21/9/18 23:36 66	23/9/18 0:41 66	24/9/18 1:46 60	25/9/18 2:51 65	26/9/18 3:56 60	
21/9/18 23:41 66 21/9/18 23:46 66	23/9/18 0:46 64 23/9/18 0:51 64	24/9/18 1:51 63 24/9/18 1:56 61	25/9/18 2:56 64 25/9/18 3:01 64	26/9/18 4:01 60 26/9/18 4:06 61	
21/9/18 23:51 66 21/9/18 23:56 66	23/9/18 0:56 64 23/9/18 1:01 64	24/9/18 2:01 60	25/9/18 3:06 64 25/9/18 3:11 64	26/9/18 4:11 61	
22/9/18 0:01 66	23/9/18 1:06 64	24/9/18 2:11 59	25/9/18 3:16 63	26/9/18 4:21 62	
22/9/18 0:06 66 22/9/18 0:11 66	23/9/18 1:11 64 23/9/18 1:16 63	24/9/18 2:16 61 24/9/18 2:21 60	25/9/18 3:21 63 25/9/18 3:26 64	26/9/18 4:26 61 26/9/18 4:31 60	
22/0/10 0.11 00	20/0/10 1.10 00	27/0/10 2.21 00	20/0/10 0.20 04	20/0/10 4.01 00	T

Real-time Noise Data Normal Day 07:00-19:0	RTN2a (Hong Ko 0 31/8/18 12:31	ng Electric Ce 64	entre) 6/9/18 7:01 63	11/9/18 13:31 67	17/9/18 8:01 60	21/9/18 14:31 64
	31/8/18 13:01	66	6/9/18 7:31 63	11/9/18 14:01 67	17/9/18 8:31 61	21/9/18 15:01 65
27/8/18 7:01 62 27/8/18 7:31 62	31/8/18 13:31 31/8/18 14:01	66 66	6/9/18 8:01 64 6/9/18 8:31 67	11/9/18 14:31 66 11/9/18 15:01 67	17/9/18 9:01 62 17/9/18 9:31 66	21/9/18 15:31 64 21/9/18 16:01 64
27/8/18 8:01 65	31/8/18 14:31		6/9/18 9:01 67	11/9/18 15:31 66	17/9/18 10:01 62	21/9/18 16:31 63
27/8/18 8:31 66	31/8/18 15:01		6/9/18 9:31 65	11/9/18 16:01 66	17/9/18 10:31 62	21/9/18 17:01 62
27/8/18 9:01 66 27/8/18 9:31 65	31/8/18 15:31 31/8/18 16:01		6/9/18 10:01 70 6/9/18 10:31 67	11/9/18 16:31 65 11/9/18 17:01 65	17/9/18 11:01 61 17/9/18 11:31 61	21/9/18 17:31 63 21/9/18 18:01 62
27/8/18 10:01 66	31/8/18 16:31	66	6/9/18 11:01 66	11/9/18 17:31 64	17/9/18 12:01 61	21/9/18 18:31 61
27/8/18 10:31 66	31/8/18 17:01		6/9/18 11:31 66	11/9/18 18:01 63	17/9/18 12:31 61	22/9/18 7:01 59
27/8/18 11:01 67 27/8/18 11:31 63	31/8/18 17:31 31/8/18 18:01	64 63	6/9/18 12:01 64 6/9/18 12:31 64	11/9/18 18:31 63 12/9/18 7:01 61	17/9/18 13:01 62 17/9/18 13:31 62	22/9/18 7:31 62 22/9/18 8:01 64
27/8/18 12:01 64	31/8/18 18:31	63	6/9/18 13:01 65	12/9/18 7:31 62	17/9/18 14:01 63	22/9/18 8:31 67
27/8/18 12:31 63 27/8/18 13:01 65	1/9/18 7:01 1/9/18 7:31	61 62	6/9/18 13:31 67 6/9/18 14:01 66	12/9/18 8:01 64 12/9/18 8:31 66	17/9/18 14:31 63 17/9/18 15:01 63	22/9/18 9:01 67 22/9/18 9:31 66
27/8/18 13:31 67	1/9/18 8:01	64	6/9/18 14:31 67	12/9/18 9:01 66	17/9/18 15:31 62	22/9/18 10:01 65
27/8/18 14:01 66	1/9/18 8:31	66	6/9/18 15:01 66	12/9/18 9:31 66	17/9/18 16:01 62	22/9/18 10:31 65
27/8/18 14:31 66 27/8/18 15:01 67	1/9/18 9:01 1/9/18 9:31	65 66	6/9/18 15:31 50 6/9/18 16:01 66	12/9/18 10:01 66 12/9/18 10:31 65	17/9/18 16:31 62 17/9/18 17:01 62	22/9/18 11:01 65 22/9/18 11:31 62
27/8/18 15:31 65	1/9/18 10:01	66	6/9/18 16:31 66	12/9/18 11:01 65	17/9/18 17:31 62	22/9/18 12:01 61
27/8/18 16:01 65 27/8/18 16:31 66	1/9/18 10:31 1/9/18 11:01	66 66	6/9/18 17:01 64 6/9/18 17:31 64	12/9/18 11:31 66 12/9/18 12:01 65	17/9/18 18:01 60 17/9/18 18:31 60	22/9/18 12:31 61 22/9/18 13:01 64
27/8/18 17:01 65	1/9/18 11:31	65	6/9/18 18:01 65	12/9/18 12:31 64	18/9/18 7:01 59	22/9/18 13:31 64
27/8/18 17:31 64	1/9/18 12:01	66	6/9/18 18:31 65 7/0/18 7:01 60	12/9/18 13:01 66	18/9/18 7:31 60	22/9/18 14:01 64
27/8/18 18:01 64 27/8/18 18:31 64	1/9/18 12:31 1/9/18 13:01	65 48	7/9/18 7:01 62 7/9/18 7:31 63	12/9/18 13:31 66 12/9/18 14:01 65	18/9/18 8:01 62 18/9/18 8:31 63	22/9/18 14:31 64 22/9/18 15:01 62
28/8/18 7:01 62	1/9/18 13:31	67	7/9/18 8:01 65	12/9/18 14:31 67	18/9/18 9:01 63	22/9/18 15:31 62
28/8/18 7:31 63 28/8/18 8:01 63	1/9/18 14:01 1/9/18 14:31	65 65	7/9/18 8:31 66 7/9/18 9:01 67	12/9/18 15:01 63 12/9/18 15:31 64	18/9/18 9:31 64 18/9/18 10:01 64	22/9/18 16:01 62 22/9/18 16:31 62
28/8/18 8:31 65	1/9/18 15:01	64	7/9/18 9:31 67	12/9/18 16:01 63	18/9/18 10:31 66	22/9/18 17:01 62
28/8/18 9:01 65 28/8/18 9:31 65	1/9/18 15:31	63 63	7/9/18 10:01 48 7/9/18 10:31 66	12/9/18 16:31 63 12/9/18 17:01 62	18/9/18 11:01 65 18/9/18 11:31 63	22/9/18 17:31 62 22/9/18 18:01 62
28/8/18 9:31 65 28/8/18 10:01 67	1/9/18 16:01 1/9/18 16:31	63 65	7/9/18 10:31 66 7/9/18 11:01 65	12/9/18 17:01 62 12/9/18 17:31 61	18/9/18 11:31 63 18/9/18 12:01 63	22/9/18 18:01 62 22/9/18 18:31 61
28/8/18 10:31 67	1/9/18 17:01	63	7/9/18 11:31 64	12/9/18 18:01 61	18/9/18 12:31 62	24/9/18 7:01 60
28/8/18 11:01 66 28/8/18 11:31 64	1/9/18 17:31 1/9/18 18:01	62 62	7/9/18 12:01 64 7/9/18 12:31 63	12/9/18 18:31 62 13/9/18 7:01 60	18/9/18 13:01 64 18/9/18 13:31 65	24/9/18 7:31 60 24/9/18 8:01 63
28/8/18 12:01 64	1/9/18 18:31	62	7/9/18 13:01 65	13/9/18 7:31 62	18/9/18 14:01 64	24/9/18 8:31 65
28/8/18 12:31 65 28/8/18 13:01 67	3/9/18 7:01 3/9/18 7:31	61 65	7/9/18 13:31 66 7/9/18 14:01 66	13/9/18 8:01 62 13/9/18 8:31 63	18/9/18 14:31 65 18/9/18 15:01 65	24/9/18 9:01 65 24/9/18 9:31 65
28/8/18 13:31 67	3/9/18 7:31	65 65	7/9/18 14:31 65	13/9/18 9:01 63	18/9/18 15:31 65	24/9/18 10:01 67
28/8/18 14:01 67	3/9/18 8:31	66	7/9/18 15:01 65	13/9/18 9:31 64	18/9/18 16:01 64	24/9/18 10:31 66
28/8/18 14:31 67 28/8/18 15:01 66	3/9/18 9:01 3/9/18 9:31	65 66	7/9/18 15:31 66 7/9/18 16:01 67	13/9/18 10:01 63 13/9/18 10:31 64	18/9/18 16:31 65 18/9/18 17:01 66	24/9/18 11:01 66 24/9/18 11:31 65
28/8/18 15:31 64	3/9/18 10:01	66	7/9/18 16:31 67	13/9/18 11:01 64	18/9/18 17:31 63	24/9/18 12:01 66
28/8/18 16:01 65 28/8/18 16:31 64	3/9/18 10:31 3/9/18 11:01	67 66	7/9/18 17:01 67 7/9/18 17:31 66	13/9/18 11:31 63 13/9/18 12:01 65	18/9/18 18:01 62 18/9/18 18:31 61	24/9/18 12:31 67 24/9/18 13:01 65
28/8/18 17:01 64	3/9/18 11:31	65	7/9/18 18:01 66	13/9/18 12:31 62	19/9/18 7:01 59	24/9/18 13:31 66
28/8/18 17:31 64	3/9/18 12:01	64	7/9/18 18:31 63	13/9/18 13:01 65	19/9/18 7:31 62	24/9/18 14:01 66
28/8/18 18:01 64 28/8/18 18:31 62	3/9/18 12:31 3/9/18 13:01	64 64	8/9/18 7:01 62 8/9/18 7:31 62	13/9/18 13:31 65 13/9/18 14:01 66	19/9/18 8:01 63 19/9/18 8:31 65	24/9/18 14:31 59 24/9/18 15:01 67
29/8/18 7:01 61	3/9/18 13:31	66	8/9/18 8:01 64	13/9/18 14:31 53	19/9/18 9:01 66	24/9/18 15:31 64
29/8/18 7:31 62 29/8/18 8:01 64	3/9/18 14:01 3/9/18 14:31	66 66	8/9/18 8:31 66 8/9/18 9:01 67	13/9/18 15:01 64 13/9/18 15:31 64	19/9/18 9:31 57 19/9/18 10:01 57	24/9/18 16:01 63 24/9/18 16:31 65
29/8/18 8:31 65	3/9/18 15:01	66	8/9/18 9:31 65	13/9/18 16:01 65	19/9/18 10:31 66	24/9/18 17:01 64
29/8/18 9:01 65 29/8/18 9:31 65	3/9/18 15:31 3/9/18 16:01	66	8/9/18 10:01 65 8/0/18 10:21 66	13/9/18 16:31 66	19/9/18 11:01 65 19/9/18 11:31 62	24/9/18 17:31 64 24/9/18 18:01 64
29/8/18 9:31 65 29/8/18 10:01 65	3/9/18 16:01	66 66	8/9/18 10:31 66 8/9/18 11:01 65	13/9/18 17:01 66 13/9/18 17:31 64	19/9/18 11:31 62 19/9/18 12:01 61	24/9/18 18:01 64 24/9/18 18:31 64
29/8/18 10:31 66	3/9/18 17:01	65	8/9/18 11:31 64	13/9/18 18:01 62	19/9/18 12:31 62	26/9/18 7:01 62
29/8/18 11:01 67 29/8/18 11:31 65	3/9/18 17:31 3/9/18 18:01	64 64	8/9/18 12:01 64 8/9/18 12:31 64	13/9/18 18:31 62 14/9/18 7:01 59	19/9/18 13:01 65 19/9/18 13:31 66	26/9/18 7:31 62 26/9/18 8:01 63
29/8/18 12:01 64	3/9/18 18:31	64	8/9/18 13:01 66	14/9/18 7:31 62	19/9/18 14:01 67	26/9/18 8:31 65
29/8/18 12:31 56 29/8/18 13:01 66	4/9/18 7:01 4/9/18 7:31	62 63	8/9/18 13:31 67 8/9/18 14:01 66	14/9/18 8:01 62 14/9/18 8:31 64	19/9/18 14:31 66 19/9/18 15:01 64	26/9/18 9:01 66 26/9/18 9:31 65
29/8/18 13:31 66	4/9/18 8:01	64	8/9/18 14:01 65	14/9/18 9:01 66	19/9/18 15:31 63	26/9/18 10:01 65
29/8/18 14:01 66	4/9/18 8:31	67	8/9/18 15:01 64	14/9/18 9:31 64	19/9/18 16:01 64	26/9/18 10:31 66
29/8/18 14:31 67 29/8/18 15:01 65	4/9/18 9:01 4/9/18 9:31	68 64	8/9/18 15:31 65 8/9/18 16:01 65	14/9/18 10:01 67 14/9/18 10:31 66	19/9/18 16:31 63 19/9/18 17:01 64	26/9/18 11:01 67 26/9/18 11:31 67
29/8/18 15:31 65	4/9/18 10:01	60	8/9/18 16:31 65	14/9/18 11:01 64	19/9/18 17:31 61	26/9/18 12:01 64
29/8/18 16:01 65 29/8/18 16:31 65	4/9/18 10:31 4/9/18 11:01	67 51	8/9/18 17:01 64 8/9/18 17:31 63	14/9/18 11:31 64 14/9/18 12:01 62	19/9/18 18:01 62 19/9/18 18:31 61	26/9/18 12:31 64 26/9/18 13:01 65
29/8/18 17:01 65	4/9/18 11:31	66	8/9/18 18:01 62	14/9/18 12:31 61	20/9/18 7:01 59	26/9/18 13:31 66
29/8/18 17:31 64	4/9/18 12:01	65	8/9/18 18:31 63	14/9/18 13:01 63	20/9/18 7:31 61	26/9/18 14:01 66
29/8/18 18:01 63 29/8/18 18:31 63	4/9/18 12:31 4/9/18 13:01	65 66	10/9/18 7:01 61 10/9/18 7:31 61	14/9/18 13:31 65 14/9/18 14:01 65	20/9/18 8:01 62 20/9/18 8:31 64	26/9/18 14:31 66 26/9/18 15:01 65
30/8/18 7:01 61	4/9/18 13:31	55	10/9/18 8:01 64	14/9/18 14:31 66	20/9/18 9:01 64	26/9/18 15:31 65
30/8/18 7:31 62 30/8/18 8:01 64	4/9/18 14:01 4/9/18 14:31	62 67	10/9/18 8:31 65 10/9/18 9:01 66	14/9/18 15:01 65 14/9/18 15:31 64	20/9/18 9:31 65 20/9/18 10:01 65	26/9/18 16:01 65 26/9/18 16:31 65
30/8/18 8:31 65	4/9/18 15:01	67	10/9/18 9:31 65	14/9/18 16:01 64	20/9/18 10:31 67	26/9/18 17:01 64
30/8/18 9:01 65 30/8/18 9:31 65	4/9/18 15:31 4/9/18 16:01	66 66	10/9/18 10:01 65 10/9/18 10:31 65	14/9/18 16:31 65 14/9/18 17:01 63	20/9/18 11:01 66 20/9/18 11:31 64	26/9/18 17:31 64 26/9/18 18:01 64
30/8/18 9:31 65	4/9/18 16:01 4/9/18 16:31	66	10/9/18 10:31 65	14/9/18 17:01 63 14/9/18 17:31 62	20/9/18 11:31 64 20/9/18 12:01 62	26/9/18 18:01 64 26/9/18 18:31 63
30/8/18 10:31 65	4/9/18 17:01	65	10/9/18 11:31 64	14/9/18 18:01 62	20/9/18 12:31 62	
30/8/18 11:01 64 30/8/18 11:31 64	4/9/18 17:31 4/9/18 18:01	65 65	10/9/18 12:01 64 10/9/18 12:31 64	14/9/18 18:31 61 15/9/18 7:01 59	20/9/18 13:01 64 20/9/18 13:31 65	Normal Day 19:00-23:00, Sunday & Holiday
30/8/18 12:01 63	4/9/18 18:31	65	10/9/18 13:01 64	15/9/18 7:31 60	20/9/18 14:01 65	<u>07:00-23:00</u>
30/8/18 12:31 63 30/8/18 13:01 65	5/9/18 7:01 5/9/18 7:31	61 62	10/9/18 13:31 65 10/9/18 14:01 65	15/9/18 8:01 61 15/9/18 8:31 63	20/9/18 14:31 64 20/9/18 15:01 63	27/8/18 19:01 58
30/8/18 13:31 65	5/9/18 8:01	64	10/9/18 14:31 65	15/9/18 9:01 63	20/9/18 15:31 65	27/8/18 19:06 57
30/8/18 14:01 66	5/9/18 8:31	66 67	10/9/18 15:01 65	15/9/18 9:31 63	20/9/18 16:01 64	27/8/18 19:11 57
30/8/18 14:31 65 30/8/18 15:01 66	5/9/18 9:01 5/9/18 9:31	67 68	10/9/18 15:31 65 10/9/18 16:01 65	15/9/18 10:01 62 15/9/18 10:31 63	20/9/18 16:31 63 20/9/18 17:01 62	27/8/18 19:16 55 27/8/18 19:21 58
30/8/18 15:31 66	5/9/18 10:01	67	10/9/18 16:31 65	15/9/18 11:01 63	20/9/18 17:31 61	27/8/18 19:26 57
30/8/18 16:01 65 30/8/18 16:31 66	5/9/18 10:31 5/9/18 11:01	67 59	10/9/18 17:01 66 10/9/18 17:31 65	15/9/18 11:31 64 15/9/18 12:01 62	20/9/18 18:01 61 20/9/18 18:31 61	27/8/18 19:31 58 27/8/18 19:36 59
30/8/18 17:01 64	5/9/18 11:31	66	10/9/18 18:01 64	15/9/18 12:31 61	21/9/18 7:01 60	27/8/18 19:41 59
30/8/18 17:31 64 30/8/18 18:01 64	5/9/18 12:01 5/9/18 12:31	64 64	10/9/18 18:31 63 11/9/18 7:01 62	15/9/18 13:01 62 15/9/18 13:31 62	21/9/18 7:31 61 21/9/18 8:01 63	27/8/18 19:46 59 27/8/18 19:51 57
30/8/18 18:31 64	5/9/18 13:01	64 66	11/9/18 7:31 63	15/9/18 14:01 63	21/9/18 8:31 63	27/8/18 19:56 52
31/8/18 7:01 62	5/9/18 13:31	58	11/9/18 8:01 65	15/9/18 14:31 62	21/9/18 9:01 64	27/8/18 20:01 54
31/8/18 7:31 62 31/8/18 8:01 64	5/9/18 14:01 5/9/18 14:31	62 59	11/9/18 8:31 67 11/9/18 9:01 60	15/9/18 15:01 62 15/9/18 15:31 64	21/9/18 9:31 65 21/9/18 10:01 65	27/8/18 20:06 56 27/8/18 20:11 58
31/8/18 8:31 66	5/9/18 15:01	56	11/9/18 9:31 60	15/9/18 16:01 63	21/9/18 10:31 65	27/8/18 20:16 56
31/8/18 9:01 66 31/8/18 9:31 67	5/9/18 15:31 5/9/18 16:01	67 66	11/9/18 10:01 66 11/9/18 10:31 66	15/9/18 16:31 62 15/9/18 17:01 62	21/9/18 11:01 64 21/9/18 11:31 63	27/8/18 20:21 55 27/8/18 20:26 57
31/8/18 10:01 67	5/9/18 16:01	66 67	11/9/18 11:01 66	15/9/18 17:31 61	21/9/18 12:01 62	27/8/18 20:31 56
31/8/18 10:31 67	5/9/18 17:01	67 66	11/9/18 11:31 65	15/9/18 18:01 60	21/9/18 12:31 62	27/8/18 20:36 51
31/8/18 11:01 66 31/8/18 11:31 64	5/9/18 17:31 5/9/18 18:01	66 64	11/9/18 12:01 65 11/9/18 12:31 65	15/9/18 18:31 61 17/9/18 7:01 57	21/9/18 13:01 63 21/9/18 13:31 64	27/8/18 20:41 55 27/8/18 20:46 61
31/8/18 12:01 64	5/9/18 18:31	64	11/9/18 13:01 66	17/9/18 7:31 59	21/9/18 14:01 64	27/8/18 20:51 62

27/8/18 20:56 27/8/18 21:01	<u>9 Data</u> 56 58	RTN2a (Hong Kong Electric C 29/8/18 22:01 61 29/8/18 22:06 61	<u>centre)</u> 1/9/18 19:06 61 1/9/18 19:11 61	2/9/18 12:11 60 2/9/18 12:16 61	2/9/18 21:16 61 2/9/18 21:21 62	4/9/18 22:21 61 4/9/18 22:26 61
27/8/18 21:06	57	29/8/18 22:11 61	1/9/18 19:16 61	2/9/18 12:21 62	2/9/18 21:26 55	4/9/18 22:31 62
27/8/18 21:11 27/8/18 21:16	56 58	29/8/18 22:16 61 29/8/18 22:21 61	1/9/18 19:21 61 1/9/18 19:26 61	2/9/18 12:26 49 2/9/18 12:31 62	2/9/18 21:31 61 2/9/18 21:36 62	4/9/18 22:36 62 4/9/18 22:41 61
27/8/18 21:21	57	29/8/18 22:26 61	1/9/18 19:31 61	2/9/18 12:36 61	2/9/18 21:41 63	4/9/18 22:46 61
27/8/18 21:26	56	29/8/18 22:31 61	1/9/18 19:36 61	2/9/18 12:41 51	2/9/18 21:46 61	4/9/18 22:51 61
27/8/18 21:31 27/8/18 21:36	56 57	29/8/18 22:36 61 29/8/18 22:41 61	1/9/18 19:41 61 1/9/18 19:46 61	2/9/18 12:46 62 2/9/18 12:51 50	2/9/18 21:51 61 2/9/18 21:56 62	4/9/18 22:56 61 5/9/18 19:01 60
27/8/18 21:41	62	29/8/18 22:46 61	1/9/18 19:51 61	2/9/18 12:56 61	2/9/18 22:01 50	5/9/18 19:06 58
27/8/18 21:46	61	29/8/18 22:51 63	1/9/18 19:56 61	2/9/18 13:01 55	2/9/18 22:06 61	5/9/18 19:11 58
27/8/18 21:51 27/8/18 21:56	43 56	29/8/18 22:56 54 30/8/18 19:01 56	1/9/18 20:01 61 1/9/18 20:06 60	2/9/18 13:06 56 2/9/18 13:11 55	2/9/18 22:11 61 2/9/18 22:16 61	5/9/18 19:16 57 5/9/18 19:21 53
27/8/18 22:01	53	30/8/18 19:06 58	1/9/18 20:11 61	2/9/18 13:16 62	2/9/18 22:21 61	5/9/18 19:26 59
27/8/18 22:06 27/8/18 22:11	55 58	30/8/18 19:11 57 30/8/18 19:16 55	1/9/18 20:16 61 1/9/18 20:21 61	2/9/18 13:21 43 2/9/18 13:26 65	2/9/18 22:26 61 2/9/18 22:31 61	5/9/18 19:31 58 5/9/18 19:36 59
27/8/18 22:16	54	30/8/18 19:21 54	1/9/18 20:26 61	2/9/18 13:31 61	2/9/18 22:36 61	5/9/18 19:41 59
27/8/18 22:21	56	30/8/18 19:26 58	1/9/18 20:31 61	2/9/18 13:36 61	2/9/18 22:41 61	5/9/18 19:46 59
27/8/18 22:26 27/8/18 22:31	59 56	30/8/18 19:31 56 30/8/18 19:36 62	1/9/18 20:36 61 1/9/18 20:41 61	2/9/18 13:41 51 2/9/18 13:46 52	2/9/18 22:46 61 2/9/18 22:51 60	5/9/18 19:51 59 5/9/18 19:56 58
27/8/18 22:36	51	30/8/18 19:41 62	1/9/18 20:46 61	2/9/18 13:51 62	2/9/18 22:56 61	5/9/18 20:01 58
27/8/18 22:41 27/8/18 22:46	59 52	30/8/18 19:46 48 30/8/18 19:51 50	1/9/18 20:51 61 1/9/18 20:56 61	2/9/18 13:56 61 2/9/18 14:01 61	3/9/18 19:01 58 3/9/18 19:06 57	5/9/18 20:06 61 5/9/18 20:11 56
27/8/18 22:51	53	30/8/18 19:56 54	1/9/18 21:01 61	2/9/18 14:06 61	3/9/18 19:10 57	5/9/18 20:16 53
27/8/18 22:56	61	30/8/18 20:01 51	1/9/18 21:06 60	2/9/18 14:11 61	3/9/18 19:16 56	5/9/18 20:21 61
28/8/18 19:01 28/8/18 19:06	54 62	30/8/18 20:06 49 30/8/18 20:11 61	1/9/18 21:11 60 1/9/18 21:16 60	2/9/18 14:16 61 2/9/18 14:21 64	3/9/18 19:21 57 3/9/18 19:26 56	5/9/18 20:26 55 5/9/18 20:31 55
28/8/18 19:11	62	30/8/18 20:16 62	1/9/18 21:21 61	2/9/18 14:26 61	3/9/18 19:31 57	5/9/18 20:36 61
28/8/18 19:16 28/8/18 19:21	62 62	30/8/18 20:21 62 30/8/18 20:26 43	1/9/18 21:26 61 1/9/18 21:31 62	2/9/18 14:31 61 2/9/18 14:36 61	3/9/18 19:36 60 3/9/18 19:41 63	5/9/18 20:41 56 5/9/18 20:46 57
28/8/18 19:26	62	30/8/18 20:31 39	1/9/18 21:31 02	2/9/18 14:30 61	3/9/18 19:46 59	5/9/18 20:51 58
28/8/18 19:31	62	30/8/18 20:36 53	1/9/18 21:41 60	2/9/18 14:46 61	3/9/18 19:51 64	5/9/18 20:56 56
28/8/18 19:36 28/8/18 19:41	62 52	30/8/18 20:41 62 30/8/18 20:46 61	1/9/18 21:46 62 1/9/18 21:51 61	2/9/18 14:51 62 2/9/18 14:56 61	3/9/18 19:56 61 3/9/18 20:01 61	5/9/18 21:01 59 5/9/18 21:06 63
28/8/18 19:46	49	30/8/18 20:51 61	1/9/18 21:56 59	2/9/18 15:01 61	3/9/18 20:06 61	5/9/18 21:11 59
28/8/18 19:51 28/8/18 19:56	47 61	30/8/18 20:56 61 30/8/18 21:01 61	1/9/18 22:01 62 1/9/18 22:06 61	2/9/18 15:06 61 2/9/18 15:11 61	3/9/18 20:11 62 3/9/18 20:16 52	5/9/18 21:16 58 5/9/18 21:21 60
28/8/18 20:01	61	30/8/18 21:06 61	1/9/18 22:11 55	2/9/18 15:16 61	3/9/18 20:21 46	5/9/18 21:26 56
28/8/18 20:06	61	30/8/18 21:11 52	1/9/18 22:16 62	2/9/18 15:21 62	3/9/18 20:26 50	5/9/18 21:31 56
28/8/18 20:11 28/8/18 20:16	62 48	30/8/18 21:16 51 30/8/18 21:21 61	1/9/18 22:21 61 1/9/18 22:26 61	2/9/18 15:26 53 2/9/18 15:31 61	3/9/18 20:31 54 3/9/18 20:36 53	5/9/18 21:36 57 5/9/18 21:41 56
28/8/18 20:21	62	30/8/18 21:26 61	1/9/18 22:31 62	2/9/18 15:36 63	3/9/18 20:41 61	5/9/18 21:46 61
28/8/18 20:26 28/8/18 20:31	61 62	30/8/18 21:31 61 30/8/18 21:36 61	1/9/18 22:36 61 1/9/18 22:41 46	2/9/18 15:41 61 2/9/18 15:46 62	3/9/18 20:46 61 3/9/18 20:51 58	5/9/18 21:51 58 5/9/18 21:56 59
28/8/18 20:36	54	30/8/18 21:41 61	1/9/18 22:46 61	2/9/18 15:51 62	3/9/18 20:56 59	5/9/18 22:01 55
28/8/18 20:41	62	30/8/18 21:46 61	1/9/18 22:51 62	2/9/18 15:56 62	3/9/18 21:01 48	5/9/18 22:06 56
28/8/18 20:46 28/8/18 20:51	61 61	30/8/18 21:51 61 30/8/18 21:56 61	1/9/18 22:56 61 2/9/18 7:01 60	2/9/18 16:01 57 2/9/18 16:06 61	3/9/18 21:06 61 3/9/18 21:11 61	5/9/18 22:11 59 5/9/18 22:16 56
28/8/18 20:56	61	30/8/18 22:01 52	2/9/18 7:06 60	2/9/18 16:11 62	3/9/18 21:16 61	5/9/18 22:21 57
28/8/18 21:01 28/8/18 21:06	61 61	30/8/18 22:06 61 30/8/18 22:11 61	2/9/18 7:11 51 2/9/18 7:16 60	2/9/18 16:16 52 2/9/18 16:21 55	3/9/18 21:21 61 3/9/18 21:26 61	5/9/18 22:26 57 5/9/18 22:31 55
28/8/18 21:11	61	30/8/18 22:16 61	2/9/18 7:21 60	2/9/18 16:26 64	3/9/18 21:31 61	5/9/18 22:36 54
28/8/18 21:16	61	30/8/18 22:21 61	2/9/18 7:26 60	2/9/18 16:31 57	3/9/18 21:36 61	5/9/18 22:41 55
28/8/18 21:21 28/8/18 21:26	61 61	30/8/18 22:26 61 30/8/18 22:31 61	2/9/18 7:31 60 2/9/18 7:36 60	2/9/18 16:36 61 2/9/18 16:41 57	3/9/18 21:41 61 3/9/18 21:46 61	5/9/18 22:46 54 5/9/18 22:51 56
28/8/18 21:31	61	30/8/18 22:36 62	2/9/18 7:41 60	2/9/18 16:46 62	3/9/18 21:51 61	5/9/18 22:56 58
28/8/18 21:36 28/8/18 21:41	61 61	30/8/18 22:41 61 30/8/18 22:46 61	2/9/18 7:46 60 2/9/18 7:51 60	2/9/18 16:51 46 2/9/18 16:56 52	3/9/18 21:56 61 3/9/18 22:01 61	6/9/18 19:01 62 6/9/18 19:06 62
28/8/18 21:46	61	30/8/18 22:51 61	2/9/18 7:56 61	2/9/18 17:01 52	3/9/18 22:06 61	6/9/18 19:11 63
28/8/18 21:51 28/8/18 21:56	61 61	30/8/18 22:56 61 31/8/18 19:01 55	2/9/18 8:01 61 2/9/18 8:06 61	2/9/18 17:06 62 2/9/18 17:11 62	3/9/18 22:11 61 3/9/18 22:16 61	6/9/18 19:16 58 6/9/18 19:21 56
28/8/18 22:01	61	31/8/18 19:06 55	2/9/18 8:11 61	2/9/18 17:16 46	3/9/18 22:21 62	6/9/18 19:26 58
28/8/18 22:06	61	31/8/18 19:11 55	2/9/18 8:16 58	2/9/18 17:21 55	3/9/18 22:26 62	6/9/18 19:31 56
28/8/18 22:11 28/8/18 22:16	61 61	31/8/18 19:16 55 31/8/18 19:21 52	2/9/18 8:21 61 2/9/18 8:26 56	2/9/18 17:26 46 2/9/18 17:31 53	3/9/18 22:31 61 3/9/18 22:36 62	6/9/18 19:36 56 6/9/18 19:41 59
28/8/18 22:21	61	31/8/18 19:26 62	2/9/18 8:31 61	2/9/18 17:36 62	3/9/18 22:41 61	6/9/18 19:46 53
28/8/18 22:26 28/8/18 22:31	62 61	31/8/18 19:31 55 31/8/18 19:36 59	2/9/18 8:36 61 2/9/18 8:41 44	2/9/18 17:41 54 2/9/18 17:46 61	3/9/18 22:46 61 3/9/18 22:51 61	6/9/18 19:51 61 6/9/18 19:56 53
28/8/18 22:36	61	31/8/18 19:41 59	2/9/18 8:46 54	2/9/18 17:51 62	3/9/18 22:56 61	6/9/18 20:01 60
28/8/18 22:41 28/8/18 22:46	61	31/8/18 19:46 57	2/9/18 8:51 51	2/9/18 17:56 62	4/9/18 19:01 65	6/9/18 20:06 60
28/8/18 22:51	61 61	31/8/18 19:51 56 31/8/18 19:56 54	2/9/18 8:56 61 2/9/18 9:01 61	2/9/18 18:01 59 2/9/18 18:06 57	4/9/18 19:06 62 4/9/18 19:11 59	6/9/18 20:11 59 6/9/18 20:16 59
28/8/18 22:56	61	31/8/18 20:01 59	2/9/18 9:06 61	2/9/18 18:11 50	4/9/18 19:16 58	6/9/18 20:21 58
29/8/18 19:01 29/8/18 19:06	62 61	31/8/18 20:06 55 31/8/18 20:11 57	2/9/18 9:11 60 2/9/18 9:16 61	2/9/18 18:16 50 2/9/18 18:21 57	4/9/18 19:21 64 4/9/18 19:26 58	6/9/18 20:26 59 6/9/18 20:31 59
29/8/18 19:11	58	31/8/18 20:16 56	2/9/18 9:21 61	2/9/18 18:26 54	4/9/18 19:31 59	6/9/18 20:36 57
29/8/18 19:16 29/8/18 19:21	57	31/8/18 20:21 59	2/9/18 9:26 60	2/9/18 18:31 57	4/9/18 19:36 58	6/9/18 20:41 58
29/8/18 19:26	57 56	31/8/18 20:26 57 31/8/18 20:31 59	2/9/18 9:31 60 2/9/18 9:36 61	2/9/18 18:36 62 2/9/18 18:41 62	4/9/18 19:41 61 4/9/18 19:46 62	6/9/18 20:46 59 6/9/18 20:51 57
29/8/18 19:31	55	31/8/18 20:36 60	2/9/18 9:41 60	2/9/18 18:46 62	4/9/18 19:51 56	6/9/18 20:56 59
29/8/18 19:36 29/8/18 19:41	56 57	31/8/18 20:41 56 31/8/18 20:46 55	2/9/18 9:46 60 2/9/18 9:51 61	2/9/18 18:51 61 2/9/18 18:56 59	4/9/18 19:56 55 4/9/18 20:01 61	6/9/18 21:01 54 6/9/18 21:06 61
29/8/18 19:46	57	31/8/18 20:51 58	2/9/18 9:56 61	2/9/18 19:01 53	4/9/18 20:06 36	6/9/18 21:11 59
29/8/18 19:51	54	31/8/18 20:56 61	2/9/18 10:01 61	2/9/18 19:06 61	4/9/18 20:11 51	6/9/18 21:16 63
29/8/18 19:56 29/8/18 20:01	54 58	31/8/18 21:01 61 31/8/18 21:06 61	2/9/18 10:06 61 2/9/18 10:11 61	2/9/18 19:11 61 2/9/18 19:16 61	4/9/18 20:16 63 4/9/18 20:21 59	6/9/18 21:21 49 6/9/18 21:26 54
29/8/18 20:06	56	31/8/18 21:11 54	2/9/18 10:16 61	2/9/18 19:21 63	4/9/18 20:26 55	6/9/18 21:31 50
29/8/18 20:11 29/8/18 20:16	57 55	31/8/18 21:16 55 31/8/18 21:21 52	2/9/18 10:21 61 2/9/18 10:26 56	2/9/18 19:26 57 2/9/18 19:31 50	4/9/18 20:31 62 4/9/18 20:36 47	6/9/18 21:36 62 6/9/18 21:41 62
29/8/18 20:21	53	31/8/18 21:26 62	2/9/18 10:26 56 2/9/18 10:31 42	2/9/18 19:31 50 2/9/18 19:36 61	4/9/18 20:36 47 4/9/18 20:41 51	6/9/18 21:46 61
29/8/18 20:26	56	31/8/18 21:31 46	2/9/18 10:36 56	2/9/18 19:41 61	4/9/18 20:46 55	6/9/18 21:51 62
29/8/18 20:31 29/8/18 20:36	57 54	31/8/18 21:36 61 31/8/18 21:41 62	2/9/18 10:41 62 2/9/18 10:46 61	2/9/18 19:46 36 2/9/18 19:51 62	4/9/18 20:51 56 4/9/18 20:56 49	6/9/18 21:56 62 6/9/18 22:01 44
29/8/18 20:41	55	31/8/18 21:46 59	2/9/18 10:51 61	2/9/18 19:56 62	4/9/18 21:01 62	6/9/18 22:06 58
29/8/18 20:46	51 61	31/8/18 21:51 61	2/9/18 10:56 61 2/9/18 11:01 61	2/9/18 20:01 43 2/9/18 20:06 50	4/9/18 21:06 62 4/9/18 21:11 62	6/9/18 22:11 62
29/8/18 20:51 29/8/18 20:56	61 61	31/8/18 21:56 61 31/8/18 22:01 62	2/9/18 11:01 61 2/9/18 11:06 43	2/9/18 20:06 50 2/9/18 20:11 61	4/9/18 21:11 62 4/9/18 21:16 62	6/9/18 22:16 61 6/9/18 22:21 53
29/8/18 21:01	61	31/8/18 22:06 61	2/9/18 11:11 62	2/9/18 20:16 46	4/9/18 21:21 39	6/9/18 22:26 57
29/8/18 21:06 29/8/18 21:11	62 62	31/8/18 22:11 61 31/8/18 22:16 62	2/9/18 11:16 62 2/9/18 11:21 61	2/9/18 20:21 61 2/9/18 20:26 52	4/9/18 21:26 62 4/9/18 21:31 62	6/9/18 22:31 51 6/9/18 22:36 61
29/8/18 21:16	52	31/8/18 22:21 61	2/9/18 11:26 58	2/9/18 20:31 61	4/9/18 21:36 39	6/9/18 22:41 51
29/8/18 21:21	50	31/8/18 22:26 61	2/9/18 11:31 53	2/9/18 20:36 61	4/9/18 21:41 56	6/9/18 22:46 62
29/8/18 21:26 29/8/18 21:31	53 54	31/8/18 22:31 53 31/8/18 22:36 61	2/9/18 11:36 61 2/9/18 11:41 62	2/9/18 20:41 54 2/9/18 20:46 53	4/9/18 21:46 42 4/9/18 21:51 40	6/9/18 22:51 54 6/9/18 22:56 49
29/8/18 21:36	62	31/8/18 22:41 56	2/9/18 11:46 61	2/9/18 20:51 54	4/9/18 21:56 46	7/9/18 19:01 58
29/8/18 21:41 29/8/18 21:46	61 61	31/8/18 22:46 62 31/8/18 22:51 62	2/9/18 11:51 62 2/9/18 11:56 43	2/9/18 20:56 61 2/9/18 21:01 61	4/9/18 22:01 62 4/9/18 22:06 61	7/9/18 19:06 59 7/9/18 19:11 56
-0/0/10 21.40	61	31/8/18 22:56 62	2/9/18 11:56 43	2/9/18 21:06 62	4/9/18 22:00 01	7/9/18 19:16 57
29/8/18 21:51 29/8/18 21:56	61	1/9/18 19:01 61	2/9/18 12:06 62	2/9/18 21:11 62	4/9/18 22:16 61	7/9/18 19:21 56

7/9/18 19:26 7/9/18 19:31	<u>9 Data</u> 54 60	RTN2a (Hong Kon 9/9/18 8:31 9/9/18 8:36	60 56	9/9/18 17:36 9/9/18 17:41	61 61	10/9/18 22:41 61 10/9/18 22:46 52	13/9/18 19:46 58 13/9/18 19:51 61	15/9/18 20:51 15/9/18 20:56	59 61
7/9/18 19:36	63	9/9/18 8:41	61	9/9/18 17:46	61	10/9/18 22:51 61	13/9/18 19:56 60	15/9/18 21:01	60
7/9/18 19:41 7/9/18 19:46	58 65	9/9/18 8:46 9/9/18 8:51	43 62	9/9/18 17:51 9/9/18 17:56	60 61	10/9/18 22:56 62 11/9/18 19:01 52	13/9/18 20:01 61 13/9/18 20:06 60	15/9/18 21:06 15/9/18 21:11	46 61
7/9/18 19:51	50	9/9/18 8:56	50	9/9/18 18:01	61	11/9/18 19:06 55	13/9/18 20:11 60	15/9/18 21:16	60
7/9/18 19:56	53	9/9/18 9:01	56	9/9/18 18:06	61	11/9/18 19:11 53	13/9/18 20:16 60	15/9/18 21:21	60
7/9/18 20:01 7/9/18 20:06	56 57	9/9/18 9:06 9/9/18 9:11	48 49	9/9/18 18:11 9/9/18 18:16	62 61	11/9/18 19:16 52 11/9/18 19:21 50	13/9/18 20:21 59 13/9/18 20:26 60	15/9/18 21:26 15/9/18 21:31	60 60
7/9/18 20:11	58	9/9/18 9:16	53	9/9/18 18:21	62	11/9/18 19:26 55	13/9/18 20:31 61	15/9/18 21:36	61
7/9/18 20:16	56	9/9/18 9:21	50	9/9/18 18:26	60	11/9/18 19:31 49	13/9/18 20:36 61	15/9/18 21:41	60
7/9/18 20:21 7/9/18 20:26	57 55	9/9/18 9:26 9/9/18 9:31	49 62	9/9/18 18:31 9/9/18 18:36	61 61	11/9/18 19:36 62 11/9/18 19:41 55	13/9/18 20:41 61 13/9/18 20:46 60	15/9/18 21:46 15/9/18 21:51	60 60
7/9/18 20:31	53	9/9/18 9:36	62	9/9/18 18:41	61	11/9/18 19:46 58	13/9/18 20:51 57	15/9/18 21:56	60
7/9/18 20:36 7/9/18 20:41	56 57	9/9/18 9:41 9/9/18 9:46	61 60	9/9/18 18:46 9/9/18 18:51	61 61	11/9/18 19:51 58 11/9/18 19:56 58	13/9/18 20:56 59 13/9/18 21:01 60	15/9/18 22:01 15/9/18 22:06	60 62
7/9/18 20:46	61	9/9/18 9:51	60	9/9/18 18:56	62	11/9/18 20:01 61	13/9/18 21:06 60	15/9/18 22:11	61
7/9/18 20:51	52	9/9/18 9:56	60	9/9/18 19:01	61	11/9/18 20:06 61	13/9/18 21:11 59	15/9/18 22:16	60
7/9/18 20:56 7/9/18 21:01	64 61	9/9/18 10:01 9/9/18 10:06	48 61	9/9/18 19:06 9/9/18 19:11	61 60	11/9/18 20:11 61 11/9/18 20:16 52	13/9/18 21:16 59 13/9/18 21:21 60	15/9/18 22:21 15/9/18 22:26	60 60
7/9/18 21:06	58	9/9/18 10:11	60	9/9/18 19:16	62	11/9/18 20:21 58	13/9/18 21:26 60	15/9/18 22:31	60
7/9/18 21:11	57	9/9/18 10:16	61	9/9/18 19:21	54	11/9/18 20:26 59	13/9/18 21:31 59	15/9/18 22:36	60
7/9/18 21:16 7/9/18 21:21	60 61	9/9/18 10:21 9/9/18 10:26	61 61	9/9/18 19:26 9/9/18 19:31	61 61	11/9/18 20:31 55 11/9/18 20:36 62	13/9/18 21:36 59 13/9/18 21:41 60	15/9/18 22:41 15/9/18 22:46	60 59
7/9/18 21:26	56	9/9/18 10:31	61	9/9/18 19:36	60	11/9/18 20:41 61	13/9/18 21:46 59	15/9/18 22:51	60
7/9/18 21:31 7/9/18 21:36	60 52	9/9/18 10:36 9/9/18 10:41	61 60	9/9/18 19:41 9/9/18 19:46	61 61	11/9/18 20:46 60 11/9/18 20:51 62	13/9/18 21:51 59 13/9/18 21:56 59	15/9/18 22:56 16/9/18 7:01	60 57
7/9/18 21:41	62	9/9/18 10:46	53	9/9/18 19:51	61	11/9/18 20:56 60	13/9/18 22:01 61	16/9/18 7:06	57
7/9/18 21:46 7/9/18 21:51	52 52	9/9/18 10:51 9/9/18 10:56	62 61	9/9/18 19:56 9/9/18 20:01	60 61	11/9/18 21:01 39 11/9/18 21:06 61	13/9/18 22:06 60 13/9/18 22:11 62	16/9/18 7:11 16/9/18 7:16	61 67
7/9/18 21:56	62	9/9/18 11:01	61	9/9/18 20:01	60	11/9/18 21:06 81	13/9/18 22:16 60	16/9/18 7:21	64
7/9/18 22:01	61	9/9/18 11:06	62	9/9/18 20:11	60	11/9/18 21:16 61	13/9/18 22:21 59	16/9/18 7:26	63
7/9/18 22:06 7/9/18 22:11	62 56	9/9/18 11:11 9/9/18 11:16	62 61	9/9/18 20:16 9/9/18 20:21	62 60	11/9/18 21:21 61 11/9/18 21:26 61	13/9/18 22:26 60 13/9/18 22:31 62	16/9/18 7:31 16/9/18 7:36	68 69
7/9/18 22:16	58	9/9/18 11:21	48	9/9/18 20:26	60	11/9/18 21:31 61	13/9/18 22:36 59	16/9/18 7:41	66
7/9/18 22:21	44	9/9/18 11:26	60	9/9/18 20:31	61	11/9/18 21:36 60	13/9/18 22:41 61	16/9/18 7:46	62
7/9/18 22:26 7/9/18 22:31	47 61	9/9/18 11:31 9/9/18 11:36	61 61	9/9/18 20:36 9/9/18 20:41	62 61	11/9/18 21:41 61 11/9/18 21:46 62	13/9/18 22:46 60 13/9/18 22:51 60	16/9/18 7:51 16/9/18 7:56	63 59
7/9/18 22:36	62	9/9/18 11:41	60	9/9/18 20:46	61	11/9/18 21:51 60	13/9/18 22:56 59	16/9/18 8:01	65
7/9/18 22:41 7/9/18 22:46	45 62	9/9/18 11:46 9/9/18 11:51	61 61	9/9/18 20:51 9/9/18 20:56	60 65	11/9/18 21:56 61 11/9/18 22:01 60	14/9/18 19:01 61 14/9/18 19:06 61	16/9/18 8:06 16/9/18 8:11	64 59
7/9/18 22:51	62	9/9/18 11:56	60	9/9/18 21:01	64	11/9/18 22:06 61	14/9/18 19:11 61	16/9/18 8:16	63
7/9/18 22:56	62	9/9/18 12:01	61	9/9/18 21:06	58	11/9/18 22:11 61 11/9/18 22:16 62	14/9/18 19:16 60	16/9/18 8:21	63
8/9/18 19:01 8/9/18 19:06	56 50	9/9/18 12:06 9/9/18 12:11	60 61	9/9/18 21:11 9/9/18 21:16	56 63	11/9/18 22:16 62 11/9/18 22:21 60	14/9/18 19:21 60 14/9/18 19:26 62	16/9/18 8:26 16/9/18 8:31	64 66
8/9/18 19:11	61	9/9/18 12:16	51	9/9/18 21:21	62	11/9/18 22:26 60	14/9/18 19:31 61	16/9/18 8:36	62
8/9/18 19:16 8/9/18 19:21	61 61	9/9/18 12:21 9/9/18 12:26	61 42	9/9/18 21:26 9/9/18 21:31	58 56	11/9/18 22:31 60 11/9/18 22:36 62	14/9/18 19:36 52 14/9/18 19:41 61	16/9/18 8:41 16/9/18 8:46	64 58
8/9/18 19:26	61	9/9/18 12:31	62	9/9/18 21:36	50 54	11/9/18 22:41 61	14/9/18 19:46 61	16/9/18 8:51	67
8/9/18 19:31	61	9/9/18 12:36	61	9/9/18 21:41	60	11/9/18 22:46 61	14/9/18 19:51 62	16/9/18 8:56	67
8/9/18 19:36 8/9/18 19:41	61 62	9/9/18 12:41 9/9/18 12:46	61 60	9/9/18 21:46 9/9/18 21:51	62 61	11/9/18 22:51 60 11/9/18 22:56 60	14/9/18 19:56 58 14/9/18 20:01 60	16/9/18 9:01 16/9/18 9:06	67 70
8/9/18 19:46	61	9/9/18 12:51	60	9/9/18 21:56	55	12/9/18 19:01 55	14/9/18 20:06 52	16/9/18 9:11	66
8/9/18 19:51 8/9/18 19:56	62 47	9/9/18 12:56 9/9/18 13:01	58 60	9/9/18 22:01 9/9/18 22:06	55 61	12/9/18 19:06 60 12/9/18 19:11 54	14/9/18 20:11 61 14/9/18 20:16 60	16/9/18 9:16 16/9/18 9:21	70 66
8/9/18 20:01	50	9/9/18 13:06	60	9/9/18 22:11	61	12/9/18 19:16 60	14/9/18 20:21 55	16/9/18 9:26	88
8/9/18 20:06 8/9/18 20:11	62 61	9/9/18 13:11 9/9/18 13:16	60 60	9/9/18 22:16 9/9/18 22:21	51 55	12/9/18 19:21 62 12/9/18 19:26 61	14/9/18 20:26 60 14/9/18 20:31 61	16/9/18 9:31 16/9/18 9:36	73 68
8/9/18 20:16	61	9/9/18 13:21	61	9/9/18 22:26	55	12/9/18 19:31 60	14/9/18 20:36 60	16/9/18 9:41	68
8/9/18 20:21	61	9/9/18 13:26	61	9/9/18 22:31	61	12/9/18 19:36 60	14/9/18 20:41 60	16/9/18 9:46	73
8/9/18 20:26 8/9/18 20:31	56 56	9/9/18 13:31 9/9/18 13:36	60 62	9/9/18 22:36 9/9/18 22:41	61 62	12/9/18 19:41 60 12/9/18 19:46 60	14/9/18 20:46 61 14/9/18 20:51 61	16/9/18 9:51 16/9/18 9:56	72 77
8/9/18 20:36	61	9/9/18 13:41	62	9/9/18 22:46	61	12/9/18 19:51 59	14/9/18 20:56 60	16/9/18 10:01	74
8/9/18 20:41 8/9/18 20:46	54 61	9/9/18 13:46 9/9/18 13:51	60 60	9/9/18 22:51 9/9/18 22:56	61 61	12/9/18 19:56 60 12/9/18 20:01 59	14/9/18 21:01 59 14/9/18 21:06 60	16/9/18 10:06 16/9/18 10:11	77 80
8/9/18 20:51	52	9/9/18 13:56	60	10/9/18 19:01	56	12/9/18 20:06 60	14/9/18 21:11 60	16/9/18 10:16	80
8/9/18 20:56 8/9/18 21:01	61 57	9/9/18 14:01 9/9/18 14:06	61 61	10/9/18 19:06 10/9/18 19:11	54 52	12/9/18 20:11 55 12/9/18 20:16 61	14/9/18 21:16 45 14/9/18 21:21 60	16/9/18 10:21 16/9/18 10:26	81 82
8/9/18 21:06	61	9/9/18 14:11	60	10/9/18 19:16	48	12/9/18 20:21 60	14/9/18 21:26 57	16/9/18 10:31	79
8/9/18 21:11	61	9/9/18 14:16	61	10/9/18 19:21	53	12/9/18 20:26 60	14/9/18 21:31 60	16/9/18 10:36	75 74
8/9/18 21:16 8/9/18 21:21	61 61	9/9/18 14:21 9/9/18 14:26	60 60	10/9/18 19:26 10/9/18 19:31	52 52	12/9/18 20:31 60 12/9/18 20:36 59	14/9/18 21:36 60 14/9/18 21:41 56	16/9/18 10:41 16/9/18 10:46	74 75
8/9/18 21:26	61	9/9/18 14:31	60	10/9/18 19:36	60	12/9/18 20:41 59	14/9/18 21:46 60	16/9/18 10:51	72
8/9/18 21:31 8/9/18 21:36	58 61	9/9/18 14:36 9/9/18 14:41	60 62	10/9/18 19:41 10/9/18 19:46	57 62	12/9/18 20:46 60 12/9/18 20:51 61	14/9/18 21:51 62 14/9/18 21:56 61	16/9/18 10:56 16/9/18 11:01	75 82
8/9/18 21:41	47	9/9/18 14:46	61	10/9/18 19:51	52	12/9/18 20:56 59	14/9/18 22:01 56	16/9/18 11:06	71
8/9/18 21:46	61	9/9/18 14:51	60	10/9/18 19:56	52	12/9/18 21:01 59	14/9/18 22:06 58	16/9/18 11:11	74 73
8/9/18 21:51 8/9/18 21:56	61 62	9/9/18 14:56 9/9/18 15:01	60 60	10/9/18 20:01 10/9/18 20:06	48 50	12/9/18 21:06 59 12/9/18 21:11 59	14/9/18 22:11 60 14/9/18 22:16 61	16/9/18 11:16 16/9/18 11:21	72
8/9/18 22:01	62	9/9/18 15:06	62	10/9/18 20:11	55	12/9/18 21:16 59	14/9/18 22:21 61	16/9/18 11:26	73
8/9/18 22:06 8/9/18 22:11	61 61	9/9/18 15:11 9/9/18 15:16	60 61	10/9/18 20:16 10/9/18 20:21	52 59	12/9/18 21:21 60 12/9/18 21:26 59	14/9/18 22:26 61 14/9/18 22:31 60	16/9/18 11:31 16/9/18 11:36	72 71
8/9/18 22:16	61	9/9/18 15:21	61	10/9/18 20:26	51	12/9/18 21:31 39	14/9/18 22:36 60	16/9/18 11:41	72
8/9/18 22:21 8/9/18 22:26	61 60	9/9/18 15:26 9/9/18 15:31	61 62	10/9/18 20:31 10/9/18 20:36	63 56	12/9/18 21:36 60 12/9/18 21:41 59	14/9/18 22:41 60 14/9/18 22:46 59	16/9/18 11:46 16/9/18 11:51	74 75
8/9/18 22:31	61	9/9/18 15:36	61	10/9/18 20:41	57	12/9/18 21:46 60	14/9/18 22:51 59	16/9/18 11:56	75 77
8/9/18 22:36	61	9/9/18 15:41	60	10/9/18 20:46	61	12/9/18 21:51 59	14/9/18 22:56 61	16/9/18 12:01	74
8/9/18 22:41 8/9/18 22:46	61 61	9/9/18 15:46 9/9/18 15:51	61 60	10/9/18 20:51 10/9/18 20:56	61 55	12/9/18 21:56 59 12/9/18 22:01 61	15/9/18 19:01 62 15/9/18 19:06 60	16/9/18 12:06 16/9/18 12:11	74 73
8/9/18 22:51	60	9/9/18 15:56	60	10/9/18 21:01	61	12/9/18 22:06 60	15/9/18 19:11 59	16/9/18 12:16	74 75
8/9/18 22:56 9/9/18 7:01	61 59	9/9/18 16:01 9/9/18 16:06	61 60	10/9/18 21:06 10/9/18 21:11	48 47	12/9/18 22:11 59 12/9/18 22:16 59	15/9/18 19:16 59 15/9/18 19:21 60	16/9/18 12:21 16/9/18 12:26	75 74
9/9/18 7:06	59	9/9/18 16:11	60	10/9/18 21:16	62	12/9/18 22:21 60	15/9/18 19:26 59	16/9/18 12:31	74 77
9/9/18 7:11 9/9/18 7:16	61 59	9/9/18 16:16 9/9/18 16:21	60 60	10/9/18 21:21 10/9/18 21:26	61 61	12/9/18 22:26 60 12/9/18 22:31 59	15/9/18 19:31 59 15/9/18 19:36 60	16/9/18 12:36 16/9/18 12:41	73 76
9/9/18 7:16 9/9/18 7:21	59 59	9/9/18 16:21 9/9/18 16:26	60 60	10/9/18 21:26	61	12/9/18 22:31 59 12/9/18 22:36 59	15/9/18 19:36 60 15/9/18 19:41 60	16/9/18 12:41	74
9/9/18 7:26	60	9/9/18 16:31	60	10/9/18 21:36	61	12/9/18 22:41 59	15/9/18 19:46 59	16/9/18 12:51	70
9/9/18 7:31 9/9/18 7:36	60 60	9/9/18 16:36 9/9/18 16:41	60 60	10/9/18 21:41 10/9/18 21:46	46 61	12/9/18 22:46 59 12/9/18 22:51 61	15/9/18 19:51 59 15/9/18 19:56 59	16/9/18 12:56 16/9/18 13:01	71 69
9/9/18 7:41	62	9/9/18 16:46	60	10/9/18 21:51	47	12/9/18 22:56 59	15/9/18 20:01 60	16/9/18 13:06	73
9/9/18 7:46	60	9/9/18 16:51	60	10/9/18 21:56	61	13/9/18 19:01 55	15/9/18 20:06 59	16/9/18 13:11	66
9/9/18 7:51 9/9/18 7:56	60 62	9/9/18 16:56 9/9/18 17:01	61 61	10/9/18 22:01 10/9/18 22:06	61 42	13/9/18 19:06 61 13/9/18 19:11 61	15/9/18 20:11 60 15/9/18 20:16 59	16/9/18 13:16 16/9/18 13:21	71 69
9/9/18 8:01	62	9/9/18 17:06	61	10/9/18 22:11	61	13/9/18 19:16 64	15/9/18 20:21 60	16/9/18 13:26	75
9/9/18 8:06 9/9/18 8:11	60 60	9/9/18 17:11 9/9/18 17:16	61 61	10/9/18 22:16 10/9/18 22:21	61 61	13/9/18 19:21 62 13/9/18 19:26 61	15/9/18 20:26 60 15/9/18 20:31 59	16/9/18 13:31 16/9/18 13:36	67 66
9/9/18 8:11 9/9/18 8:16	60 60	9/9/18 17:16 9/9/18 17:21	61	10/9/18 22:26	61	13/9/18 19:26 61	15/9/18 20:31 59	16/9/18 13:36	71
	60	9/9/18 17:26	60	10/9/18 22:31	62	13/9/18 19:36 63	15/9/18 20:41 60	16/9/18 13:46	71
9/9/18 8:21 9/9/18 8:26	60	9/9/18 17:31	60	10/9/18 22:36	61	13/9/18 19:41 62	15/9/18 20:46 59	16/9/18 13:51	64

16/9/18 13:56 16/9/18 14:01	<u>Data</u> 70 68	RTN2a (Hong Kong Elect 17/9/18 19:01 62 17/9/18 19:06 59	19/9/18 20:06 60 19/9/18 20:11 60	21/9/18 21:11 62 21/9/18 21:16 61	23/9/18 10:16 59 23/9/18 10:21 60	23/9/18 19:21 60 23/9/18 19:26 51
16/9/18 14:06	65	17/9/18 19:11 59	19/9/18 20:16 61	21/9/18 21:21 54	23/9/18 10:26 59	23/9/18 19:31 60
16/9/18 14:11 16/9/18 14:16	64 63	17/9/18 19:16 59 17/9/18 19:21 59	19/9/18 20:21 62 19/9/18 20:26 61	21/9/18 21:26 61 21/9/18 21:31 59	23/9/18 10:31 61 23/9/18 10:36 62	23/9/18 19:36 62 23/9/18 19:41 60
16/9/18 14:21	62	17/9/18 19:26 60	19/9/18 20:31 60	21/9/18 21:36 60	23/9/18 10:41 60	23/9/18 19:46 61
16/9/18 14:26 16/9/18 14:31	64 58	17/9/18 19:31 59 17/9/18 19:36 59	19/9/18 20:36 61 19/9/18 20:41 60	21/9/18 21:41 61 21/9/18 21:46 61	23/9/18 10:46 61 23/9/18 10:51 60	23/9/18 19:51 60 23/9/18 19:56 61
16/9/18 14:36	65	17/9/18 19:41 60	19/9/18 20:41 60	21/9/18 21:40 61	23/9/18 10:56 59	23/9/18 20:01 60
16/9/18 14:41	66	17/9/18 19:46 59	19/9/18 20:51 62	21/9/18 21:56 61	23/9/18 11:01 60	23/9/18 20:06 60
16/9/18 14:46 16/9/18 14:51	64 66	17/9/18 19:51 59 17/9/18 19:56 59	19/9/18 20:56 60 19/9/18 21:01 61	21/9/18 22:01 61 21/9/18 22:06 61	23/9/18 11:06 61 23/9/18 11:11 59	23/9/18 20:11 60 23/9/18 20:16 61
16/9/18 14:56	59	17/9/18 20:01 59	19/9/18 21:06 62	21/9/18 22:11 58	23/9/18 11:16 59	23/9/18 20:21 59
16/9/18 15:01 16/9/18 15:06	64	17/9/18 20:06 60	19/9/18 21:11 61	21/9/18 22:16 61	23/9/18 11:21 59 23/9/18 11:26 59	23/9/18 20:26 50
16/9/18 15:11	66 65	17/9/18 20:11 59 17/9/18 20:16 59	19/9/18 21:16 60 19/9/18 21:21 61	21/9/18 22:21 61 21/9/18 22:26 60	23/9/18 11:26 59 23/9/18 11:31 59	23/9/18 20:31 61 23/9/18 20:36 62
16/9/18 15:16	64	17/9/18 20:21 59	19/9/18 21:26 61	21/9/18 22:31 60	23/9/18 11:36 59	23/9/18 20:41 60
16/9/18 15:21 16/9/18 15:26	62 51	17/9/18 20:26 58 17/9/18 20:31 59	19/9/18 21:31 59 19/9/18 21:36 59	21/9/18 22:36 62 21/9/18 22:41 60	23/9/18 11:41 59 23/9/18 11:46 60	23/9/18 20:46 61 23/9/18 20:51 60
16/9/18 15:31	60	17/9/18 20:36 60	19/9/18 21:41 61	21/9/18 22:46 60	23/9/18 11:51 60	23/9/18 20:56 60
16/9/18 15:36 16/9/18 15:41	59 59	17/9/18 20:41 59 17/9/18 20:46 61	19/9/18 21:46 62 19/9/18 21:51 60	21/9/18 22:51 61 21/9/18 22:56 60	23/9/18 11:56 59 23/9/18 12:01 60	23/9/18 21:01 61 23/9/18 21:06 60
16/9/18 15:46	50	17/9/18 20:51 59	19/9/18 21:56 60	22/9/18 19:01 60	23/9/18 12:06 59	23/9/18 21:11 59
16/9/18 15:51 16/9/18 15:56	53 59	17/9/18 20:56 60 17/9/18 21:01 59	19/9/18 22:01 62 19/9/18 22:06 60	22/9/18 19:06 59 22/9/18 19:11 61	23/9/18 12:11 59 23/9/18 12:16 60	23/9/18 21:16 61 23/9/18 21:21 61
16/9/18 16:01	62	17/9/18 21:06 62	19/9/18 22:11 60	22/9/18 19:16 62	23/9/18 12:21 60	23/9/18 21:26 60
16/9/18 16:06	68	17/9/18 21:11 59	19/9/18 22:16 60	22/9/18 19:21 60	23/9/18 12:26 60	23/9/18 21:31 60
16/9/18 16:11 16/9/18 16:16	59 63	17/9/18 21:16 59 17/9/18 21:21 60	19/9/18 22:21 60 19/9/18 22:26 60	22/9/18 19:26 62 22/9/18 19:31 40	23/9/18 12:31 60 23/9/18 12:36 60	23/9/18 21:36 61 23/9/18 21:41 60
16/9/18 16:21	65	17/9/18 21:26 59	19/9/18 22:31 61	22/9/18 19:36 60	23/9/18 12:41 60	23/9/18 21:46 60
16/9/18 16:26 16/9/18 16:31	62 55	17/9/18 21:31 60 17/9/18 21:36 59	19/9/18 22:36 59 19/9/18 22:41 60	22/9/18 19:41 61 22/9/18 19:46 61	23/9/18 12:46 60 23/9/18 12:51 60	23/9/18 21:51 60 23/9/18 21:56 58
16/9/18 16:36	63	17/9/18 21:41 59	19/9/18 22:46 60	22/9/18 19:51 61	23/9/18 12:56 60	23/9/18 22:01 59
16/9/18 16:41	62	17/9/18 21:46 59	19/9/18 22:51 60	22/9/18 19:56 60	23/9/18 13:01 60	23/9/18 22:06 59
16/9/18 16:46 16/9/18 16:51	54 61	17/9/18 21:51 58 17/9/18 21:56 59	19/9/18 22:56 59 20/9/18 19:01 60	22/9/18 20:01 61 22/9/18 20:06 60	23/9/18 13:06 61 23/9/18 13:11 60	23/9/18 22:11 59 23/9/18 22:16 59
16/9/18 16:56	60	17/9/18 22:01 59	20/9/18 19:06 60	22/9/18 20:11 60	23/9/18 13:16 59	23/9/18 22:21 61
16/9/18 17:01 16/9/18 17:06	62 60	17/9/18 22:06 58 17/9/18 22:11 59	20/9/18 19:11 60 20/9/18 19:16 61	22/9/18 20:16 54 22/9/18 20:21 61	23/9/18 13:21 60 23/9/18 13:26 60	23/9/18 22:26 59 23/9/18 22:31 61
16/9/18 17:11	59	17/9/18 22:16 58	20/9/18 19:21 50	22/9/18 20:26 61	23/9/18 13:31 60	23/9/18 22:36 61
16/9/18 17:16 16/9/18 17:21	62 57	17/9/18 22:21 59 17/9/18 22:26 59	20/9/18 19:26 61 20/9/18 19:31 61	22/9/18 20:31 62 22/9/18 20:36 54	23/9/18 13:36 60 23/9/18 13:41 60	23/9/18 22:41 60 23/9/18 22:46 59
16/9/18 17:26	61	17/9/18 22:31 58	20/9/18 19:36 61	22/9/18 20:41 61	23/9/18 13:46 60	23/9/18 22:51 59
16/9/18 17:31 16/9/18 17:36	58 61	17/9/18 22:36 58 17/9/18 22:41 58	20/9/18 19:41 61 20/9/18 19:46 61	22/9/18 20:46 62 22/9/18 20:51 61	23/9/18 13:51 61 23/9/18 13:56 60	23/9/18 22:56 60 24/9/18 19:01 61
16/9/18 17:41	59	17/9/18 22:46 59	20/9/18 19:51 61	22/9/18 20:56 59	23/9/18 14:01 59	24/9/18 19:06 57
16/9/18 17:46	60 55	17/9/18 22:51 61	20/9/18 19:56 58	22/9/18 21:01 61	23/9/18 14:06 59	24/9/18 19:11 58
16/9/18 17:51 16/9/18 17:56	55 50	17/9/18 22:56 58 18/9/18 19:01 62	20/9/18 20:01 61 20/9/18 20:06 61	22/9/18 21:06 60 22/9/18 21:11 60	23/9/18 14:11 60 23/9/18 14:16 61	24/9/18 19:16 59 24/9/18 19:21 56
16/9/18 18:01	60	18/9/18 19:06 61	20/9/18 20:11 60	22/9/18 21:16 60	23/9/18 14:21 62	24/9/18 19:26 56
16/9/18 18:06 16/9/18 18:11	60 58	18/9/18 19:11 61 18/9/18 19:16 61	20/9/18 20:16 61 20/9/18 20:21 60	22/9/18 21:21 50 22/9/18 21:26 59	23/9/18 14:26 59 23/9/18 14:31 59	24/9/18 19:31 57 24/9/18 19:36 58
16/9/18 18:16	48	18/9/18 19:21 61	20/9/18 20:26 60	22/9/18 21:31 60	23/9/18 14:36 59	24/9/18 19:41 56
16/9/18 18:21 16/9/18 18:26	57 60	18/9/18 19:26 61 18/9/18 19:31 61	20/9/18 20:31 51 20/9/18 20:36 61	22/9/18 21:36 60 22/9/18 21:41 60	23/9/18 14:41 59 23/9/18 14:46 59	24/9/18 19:46 57 24/9/18 19:51 55
16/9/18 18:31	62	18/9/18 19:36 60	20/9/18 20:41 61	22/9/18 21:46 61	23/9/18 14:51 60	24/9/18 19:56 58
16/9/18 18:36 16/9/18 18:41	61 59	18/9/18 19:41 52 18/9/18 19:46 62	20/9/18 20:46 59 20/9/18 20:51 59	22/9/18 21:51 61 22/9/18 21:56 61	23/9/18 14:56 60 23/9/18 15:01 59	24/9/18 20:01 60 24/9/18 20:06 62
16/9/18 18:46	58	18/9/18 19:51 61	20/9/18 20:56 59	22/9/18 22:01 61	23/9/18 15:06 59	24/9/18 20:11 59
16/9/18 18:51	60 50	18/9/18 19:56 61	20/9/18 21:01 61	22/9/18 22:06 61	23/9/18 15:11 60	24/9/18 20:16 56
16/9/18 18:56 16/9/18 19:01	59 60	18/9/18 20:01 60 18/9/18 20:06 60	20/9/18 21:06 60 20/9/18 21:11 61	22/9/18 22:11 48 22/9/18 22:16 62	23/9/18 15:16 59 23/9/18 15:21 59	24/9/18 20:21 60 24/9/18 20:26 39
16/9/18 19:06	61	18/9/18 20:11 56	20/9/18 21:16 61	22/9/18 22:21 59	23/9/18 15:26 60	24/9/18 20:31 50
16/9/18 19:11 16/9/18 19:16	55 58	18/9/18 20:16 57 18/9/18 20:21 60	20/9/18 21:21 59 20/9/18 21:26 61	22/9/18 22:26 60 22/9/18 22:31 61	23/9/18 15:31 60 23/9/18 15:36 61	24/9/18 20:36 62 24/9/18 20:41 62
16/9/18 19:21	58	18/9/18 20:26 59	20/9/18 21:31 58	22/9/18 22:36 60	23/9/18 15:41 60	24/9/18 20:46 63
16/9/18 19:26 16/9/18 19:31	62 54	18/9/18 20:31 60 18/9/18 20:36 60	20/9/18 21:36 61 20/9/18 21:41 60	22/9/18 22:41 60 22/9/18 22:46 59	23/9/18 15:46 60 23/9/18 15:51 61	24/9/18 20:51 61 24/9/18 20:56 62
16/9/18 19:36	60	18/9/18 20:41 60	20/9/18 21:46 60	22/9/18 22:51 60	23/9/18 15:56 62	24/9/18 21:01 62
16/9/18 19:41 16/9/18 19:46	58 61	18/9/18 20:46 60 18/9/18 20:51 60	20/9/18 21:51 60 20/9/18 21:56 60	22/9/18 22:56 60 23/9/18 7:01 59	23/9/18 16:01 62 23/9/18 16:06 61	24/9/18 21:06 55 24/9/18 21:11 50
16/9/18 19:51	60	18/9/18 20:56 59	20/9/18 22:01 60	23/9/18 7:06 58	23/9/18 16:11 60	24/9/18 21:16 54
16/9/18 19:56 16/9/18 20:01	62 59	18/9/18 21:01 62 18/9/18 21:06 60	20/9/18 22:06 59 20/9/18 22:11 59	23/9/18 7:11 56 23/9/18 7:16 58	23/9/18 16:16 60 23/9/18 16:21 60	24/9/18 21:21 62 24/9/18 21:26 62
16/9/18 20:06	54	18/9/18 21:11 59	20/9/18 22:16 60	23/9/18 7:21 60	23/9/18 16:26 60	24/9/18 21:31 55
16/9/18 20:11	55	18/9/18 21:16 61	20/9/18 22:21 61	23/9/18 7:26 59	23/9/18 16:31 57	24/9/18 21:36 62
16/9/18 20:16 16/9/18 20:21	61 57	18/9/18 21:21 59 18/9/18 21:26 55	20/9/18 22:26 61 20/9/18 22:31 60	23/9/18 7:31 59 23/9/18 7:36 62	23/9/18 16:36 62 23/9/18 16:41 60	24/9/18 21:41 52 24/9/18 21:46 53
16/9/18 20:26	48	18/9/18 21:31 60	20/9/18 22:36 61	23/9/18 7:41 59	23/9/18 16:46 64	24/9/18 21:51 49
16/9/18 20:31 16/9/18 20:36	53 60	18/9/18 21:36 61 18/9/18 21:41 60	20/9/18 22:41 60 20/9/18 22:46 60	23/9/18 7:46 60 23/9/18 7:51 60	23/9/18 16:51 44 23/9/18 16:56 61	24/9/18 21:56 48 24/9/18 22:01 62
16/9/18 20:41	49	18/9/18 21:46 61	20/9/18 22:51 46	23/9/18 7:56 61	23/9/18 17:01 61	24/9/18 22:06 56
16/9/18 20:46 16/9/18 20:51	61 60	18/9/18 21:51 59 18/9/18 21:56 62	20/9/18 22:56 61 21/9/18 19:01 61	23/9/18 8:01 60 23/9/18 8:06 60	23/9/18 17:06 50 23/9/18 17:11 61	24/9/18 22:11 54 24/9/18 22:16 61
16/9/18 20:56	61	18/9/18 22:01 50	21/9/18 19:06 61	23/9/18 8:10 60	23/9/18 17:16 62	24/9/18 22:21 61
16/9/18 21:01	60 50	18/9/18 22:06 61	21/9/18 19:11 60	23/9/18 8:16 59	23/9/18 17:21 62 23/9/18 17:26 54	24/9/18 22:26 46
16/9/18 21:06 16/9/18 21:11	59 60	18/9/18 22:11 60 18/9/18 22:16 60	21/9/18 19:16 60 21/9/18 19:21 61	23/9/18 8:21 59 23/9/18 8:26 60	23/9/18 17:26 54 23/9/18 17:31 61	24/9/18 22:31 62 24/9/18 22:36 62
16/9/18 21:16	60	18/9/18 22:21 59	21/9/18 19:26 62	23/9/18 8:31 60	23/9/18 17:36 61	24/9/18 22:41 62
16/9/18 21:21 16/9/18 21:26	59 58	18/9/18 22:26 59 18/9/18 22:31 60	21/9/18 19:31 61 21/9/18 19:36 61	23/9/18 8:36 60 23/9/18 8:41 53	23/9/18 17:41 60 23/9/18 17:46 60	24/9/18 22:46 62 24/9/18 22:51 62
16/9/18 21:31	60	18/9/18 22:36 59	21/9/18 19:41 62	23/9/18 8:46 59	23/9/18 17:51 60	24/9/18 22:56 45
16/9/18 21:36 16/9/18 21:41	59 59	18/9/18 22:41 61 18/9/18 22:46 60	21/9/18 19:46 61 21/9/18 19:51 62	23/9/18 8:51 60 23/9/18 8:56 61	23/9/18 17:56 61 23/9/18 18:01 61	25/9/18 7:01 61 25/9/18 7:06 61
16/9/18 21:46	59	18/9/18 22:51 60	21/9/18 19:56 60	23/9/18 9:01 61	23/9/18 18:06 60	25/9/18 7:11 61
16/9/18 21:51 16/9/18 21:56	59 58	18/9/18 22:56 59 19/9/18 19:01 64	21/9/18 20:01 60 21/9/18 20:06 61	23/9/18 9:06 60 23/9/18 9:11 59	23/9/18 18:11 61 23/9/18 18:16 61	25/9/18 7:16 62 25/9/18 7:21 61
16/9/18 22:01	58	19/9/18 19:06 62	21/9/18 20:11 61	23/9/18 9:16 61	23/9/18 18:21 49	25/9/18 7:26 61
16/9/18 22:06	58	19/9/18 19:11 61	21/9/18 20:16 61	23/9/18 9:21 60	23/9/18 18:26 61	25/9/18 7:31 62
16/9/18 22:11 16/9/18 22:16	58 61	19/9/18 19:16 60 19/9/18 19:21 60	21/9/18 20:21 61 21/9/18 20:26 60	23/9/18 9:26 61 23/9/18 9:31 62	23/9/18 18:31 60 23/9/18 18:36 60	25/9/18 7:36 50 25/9/18 7:41 62
16/9/18 22:21	58	19/9/18 19:26 61	21/9/18 20:31 61	23/9/18 9:36 60	23/9/18 18:41 62	25/9/18 7:46 62
16/9/18 22:26 16/9/18 22:31	59 59	19/9/18 19:31 61 19/9/18 19:36 61	21/9/18 20:36 60 21/9/18 20:41 60	23/9/18 9:41 61 23/9/18 9:46 61	23/9/18 18:46 61 23/9/18 18:51 61	25/9/18 7:51 61 25/9/18 7:56 49
16/9/18 22:36	58	19/9/18 19:41 61	21/9/18 20:46 60	23/9/18 9:51 60	23/9/18 18:56 61	25/9/18 8:01 62
16/9/18 22:41	58 58	19/9/18 19:46 61 19/9/18 19:51 60	21/9/18 20:51 54 21/9/18 20:56 61	23/9/18 9:56 61 23/9/18 10:01 61	23/9/18 19:01 61 23/9/18 19:06 62	25/9/18 8:06 58 25/9/18 8:11 53
16/0/10 20.40		10/0/10/10/10/00/00/00/00/00/00/00/00/00	21/9/10/20:00 01			
16/9/18 22:46 16/9/18 22:51 16/9/18 22:56	57	19/9/18 19:56 60	21/9/18 21:01 52 21/9/18 21:06 60	23/9/18 10:06 61	23/9/18 19:11 62	25/9/18 8:16 57 25/9/18 8:21 56

	Real-time Noise Data	RTN2a (Hong Kong Electric Cent	re)			
	25/9/18 8:26 53	25/9/18 17:31 54	26/9/18 22:36 61			
	25/9/18 8:36 55	25/9/18 17:41 55	26/9/18 22:46 61	28/8/18 0:36 56	29/8/18 1:41 54	30/8/18 2:46 54
	25/9/18 8:51 57	25/9/18 17:56 57		28/8/18 0:51 73	29/8/18 1:56 55	30/8/18 3:01 52
			Night time: 23:00-07:00			
						30/8/18 3:16 54
	25/9/18 9:16 57	25/9/18 18:21 50	27/8/18 0:11 63	28/8/18 1:16 60	29/8/18 2:21 54	30/8/18 3:26 52
	25/9/18 9:31 59	25/9/18 18:36 54	27/8/18 0:26 63	28/8/18 1:31 58	29/8/18 2:36 55	30/8/18 3:41 53
Abs Statule 180 C. Statule 180 C. Statule 180 C. Statule 180 C. Statule 180 Statue 180	25/9/18 9:46 58	25/9/18 18:51 58	27/8/18 0:41 59	28/8/18 1:46 55	29/8/18 2:51 52	30/8/18 3:56 53
	25/9/18 9:56 56	25/9/18 19:01 55	27/8/18 0:51 58	28/8/18 1:56 55	29/8/18 3:01 53	30/8/18 4:06 52
Bergeler State	25/9/18 10:11 58	25/9/18 19:16 52	27/8/18 1:06 56	28/8/18 2:11 54	29/8/18 3:16 54	30/8/18 4:21 53
Schell Hold						
Borther Gost F. Status Borther Status Status Borther Status </td <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>						
Separation Fig. Separation Separation <td>25/9/18 10:36 57</td> <td>25/9/18 19:41 60</td> <td>27/8/18 1:31 56</td> <td>28/8/18 2:36 54</td> <td>29/8/18 3:41 64</td> <td>30/8/18 4:46 53</td>	25/9/18 10:36 57	25/9/18 19:41 60	27/8/18 1:31 56	28/8/18 2:36 54	29/8/18 3:41 64	30/8/18 4:46 53
Segne (105) Segne (105) <thsegne (105)<="" th=""> <thsegne (105)<="" th=""></thsegne></thsegne>						
Schell mit Inf C Zichel Boldin Zichel Boldin <thzichel boldin<="" th=""> Zichel Boldin <thzic< td=""><td></td><td></td><td></td><td></td><td></td><td>30/8/18 5:01 55</td></thzic<></thzichel>						30/8/18 5:01 55
					29/8/18 4:06 53	
	25/9/18 11:16 56	25/9/18 20:21 61	27/8/18 2:11 56	28/8/18 3:16 57	29/8/18 4:21 53	30/8/18 5:26 54
25/518 1151 63 25/518 23/518	25/9/18 11:41 54	25/9/18 20:46 61	27/8/18 2:36 56	28/8/18 3:41 54	29/8/18 4:46 54	30/8/18 5:51 53
25/3918 11:56 65 29/978 21:57 58 22/9718 55:58 53 22/9718 55:59 330/918 55:59						
25/5181 55 25/5181 57 25/5181 57 25/5181 57 25/5181 57 25/5181 57 25/5181 57 25/5181 57 25/5181 57 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 25/5181 56 <t< td=""><td>25/9/18 11:56 55</td><td>25/9/18 21:01 44</td><td>27/8/18 2:51 58</td><td>28/8/18 3:56 53</td><td>29/8/18 5:01 54</td><td>30/8/18 6:06 56</td></t<>	25/9/18 11:56 55	25/9/18 21:01 44	27/8/18 2:51 58	28/8/18 3:56 53	29/8/18 5:01 54	30/8/18 6:06 56
Sister is trained						
25/59181221 57 25/59181221 57 25/59181221 57 25/59181221 59 28/59184221 54 28/59184221 53 28/5918421 54 28/59184241 54 28/59184241 54 28/59184241 54 28/59184241 55 28/59184241 55 28/59184241 55 28/59184241 55 28/59184241 55 28/59184241 55 28/59184241 55 28/59184241 55 28/59184241 55 28/59184241 55 28/59184244 54 28/59184244 54 28/59184244 54 28/59184244 54 28/59184244 54 28/59184350 53 28/59184241 53 28/59184244 54 28/5918501 53 28/59184241 53 28/59184244 54 28/5918501 53 28/59184241 55 28/5918501 53 28/59185131 53 28/59185131 53 28/5918531 53 28/5918531 53 28/5918624 57 38/5918231 53 28/59186461 57 38/5918333						
Schult 12:31 56 25/01/18 2:36 62 27/201/18 2:36 30 28/01/18 5:36 30/01/18 6:41 5:36 30/01/18 6:44 5:36 30/01/18 6:44 5:36 30/01/18 6:44 5:36 30/01/18 6:44 5:36 30/01/18 6:46 5:36 30/01/18 6:56 5:37 30/01/18 6:56 5:37 30/01/18 6:56 5:37 30/01/18 5:36 30/01/18 3:37 28/01/18 5:36 30/01/18 3:37 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 6:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/18 5:36 28/01/	25/9/18 12:21 57	25/9/18 21:26 47	27/8/18 3:16 59	28/8/18 4:21 54	29/8/18 5:26 55	30/8/18 6:31 56
Schult 12:26 58 25/911 12:26 58 25/911 12:26 50 28/911 6:241 53 29/911 6:241 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:245 53 29/911 6:256 53 29/911 6:256 53 29/911 6:246 53 29/911 6:246 53 29/911 6:246 53 29/911 6:241 55 39/911 6:241 55 39/911 6:241 57 29/911 6:241 56 29/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241 57 39/911 6:241						
Schult 12:46 68 250/11 82:16 63 27/10/18 3:41 68 280/11 4:46 54 290/11 5:51 53 300/11 6:66 67 250/11 12:56 67 250/11 82:16 61 27/10/18 3:41 67 280/11 4:46 53 290/11 6:11 55 300/11 6:21 53 250/11 12:16 61 27/10/18 3:41 65 280/11 6:11 54 290/11 6:11 54 290/11 6:11 55 290/11 6:11 57 290/11 6:11 53 300/11 6:21 53 300/11 6:21 53 300/11 6:21 53 300/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 53 290/11 6:21 <td>25/9/18 12:36 58</td> <td>25/9/18 21:41 52</td> <td>27/8/18 3:31 59</td> <td>28/8/18 4:36 53</td> <td>29/8/18 5:41 53</td> <td>30/8/18 6:46 56</td>	25/9/18 12:36 58	25/9/18 21:41 52	27/8/18 3:31 59	28/8/18 4:36 53	29/8/18 5:41 53	30/8/18 6:46 56
25/018 12:56 57 25/018 3.00 15 3.00 16 27/018 5.5 2.00 3.00 15 3.00 16 3.00	25/9/18 12:46 58	25/9/18 21:51 53	27/8/18 3:41 58	28/8/18 4:46 54	29/8/18 5:51 53	30/8/18 6:56 57
25/01/10.301 58 25/01/10.306 57 25/01/10.306 57 25/01/10.306 57 25/01/10.306 57 25/01/10.306 57 25/01/10.306 57 25/01/10.306 57 25/01/10.306 57 25/01/10.306 57 25/01/10.307 57 25/01/10.307 57 25/01/10.307 57 25/01/10.307 57 25/01/10.307 57 25/01/10.307 57 25/01/10.307 57 25/01/10.307 57 25/01/10.307 57 30/01/10.231 56 52 20/						
259/01813:11 54 259/01813:11 56 259/01813:12 57 259/01813:12 57 259/01813:21 56 288/0185:21 53 288/0186:21 56 300/01822:23 60 259/01813:21 57 259/0182:23 61 27/0184:21 56 288/0185:21 53 288/0186:21 57 300/0182:23:0 59 259/01813:24 60 27/0184:21 56 288/0185:24 53 288/0186:15 57 300/0182:35:0 57 259/01813:46 60 27/0184:41 55 288/0185:41 52 288/0185:46 57 300/0182:35:0 57 259/01813:46 60 259/0182:56 57 300/0182:35:0 57 300/0182:35:0 57 259/0181:41:10 61 226/0181:01:0 58 228/018:01:0 54 228/018:01:0 54 228/018:01:0 54 28/018:01:0 57 28/018:01:0 55 28/018:01:0 54 28/018:01:0 57 30/018:02:0 59 31/018:00:0 57	25/9/18 13:01 58	25/9/18 22:06 61	27/8/18 3:56 56	28/8/18 5:01 53	29/8/18 6:06 55	30/8/18 23:11 62
259/07 259/07 259/07 228/07 55 288/07 56 57 300/07 55 288/07 56 57 300/07 55 288/07 55 288/07 56 57 300/07 56 57 300/07 56 57 300/07 56 57 300/07 56 56 288/07 56 52 288/07 57 300/07 56 58 288/07 57 300/07 56 288/07 57 300/07 50 288/07						
259/07813326 52 299/0786331 57 300/07823/08 259/0781333 67 299/078233 69 27/07184231 56 299/078531 53 299/0786331 57 300/07823/08 57 200/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 56 299/07820/078 57 399/0780/078						
259/071813:de 57 259/07182:de 54 289/07186:de1 57 300/07182:de5 57 259/07181:de 60 259/07182:de 61 277/07144:de 55 288/07185:de 54 289/07186:de 57 300/07182:de5 57 30/07182:de5 57 28/07181:de5 55 28/07184:de5 56 28/07184:de5 57 28/07184:de5 56 28/07184:de5 57 28/07184:de5 57	25/9/18 13:26 52	25/9/18 22:31 61	27/8/18 4:21 56	28/8/18 5:26 52	29/8/18 6:31 57	30/8/18 23:36 58
259/078 13:44 60 259/078 22:46 61 27/0718 4:46 54 280/078 6:56 57 30/0718 23:56 57 259/078 13:45 56 259/078 13:45 56 259/078 13:45 56 259/078 13:45 56 259/078 13:45 56 290/078 6:56 57 30/078 0:25 31/078 0:06 57 259/078 13:46 56 259/078 13:45 55 280/078 5:56 53 290/078 6:25 53 31/078 0:26 57 31/078 0:26 57 31/078 0:26 53 290/078 0:20 62 31/078 0:26 53 290/078 0:20 62 31/078 0:26 53 290/078 0:22 57 31/078 0:26 55 290/078 0:22 57 31/078 0:26 55 290/078 0:22 57 31/078 0:26 55 259/078 1:4:41 56 250/078 1:4:45 56 290/078 0:22 57 31/078 0:26 56 259/078 1:4:44 56 260/078 19:41 56 290/078 0:23 57 31/078 0:26 56 259/078 1:4:44 56						
25/9/18 13:51 56 25/9/18 13:51 53 29/9/18 55 57 31/9/18 10:01 57 25/9/18 13:06 55 22/9/18 15:55 22/9/18 55 52/9/18 23/07 59 31/9/18 50 31/9/18 50 31/9/18 50 31/9/18 50 31/9/18 50 31/9/18 50 31/9/18 50 23/9/18 51 53 23/9/18 54 23/9/18 54 23/9/18 54 23/9/18 54 23/9/18 54 23/9/18 55 23/9/18 56 23/9/18 56 23/9/18 57 31/9/18 50 23/9/18 57 31/9/18 50 23/9/18 56 23/9/18 56 23/9/18 57 31/9/18 50 23/9/18 56 23/9/18 56 23/9/18 56 23/9/18 56 23/9/18 56 23/9/18 56 23/9/18 56 23/9/18 56 23/9/18 56 2	25/9/18 13:41 60	25/9/18 22:46 61	27/8/18 4:36 54	28/8/18 5:41 52	29/8/18 6:46 56	30/8/18 23:51 57
259/18 14.01 61 269/18 199/16 209/18 220/18 150 220/18 160.01 54 299/18 230.01 62 31/0/18.01.11 57 259/18 14.11 56 269/18 191.15 57 27/018 50 220/18 65 299/18 231.01 58 31/0/18.01.21 59 259/18 14.11 56 269/18 191.22 54 27/018 51 220/18 62 299/18 232.21 58 31/0/18.01.31 57 27/018 52 28/018 62 299/18 233.36 57 31/0/18.01.31 57 27/018 53.31 56 28/018 63.31 59 299/18 234.41 58 31/0/18.01.41 57 25/0/18 14.44 56 269/18 19.45 57 27/018 5.5 28/018 64.11 57 29/018 23.36 57 31/0/18.01 57 25/0/18 14.44 56 269/18 10.62 57 28/018 66.5 29/018 23.66 57	25/9/18 13:51 56	25/9/18 22:56 62	27/8/18 4:46 55	28/8/18 5:51 53	29/8/18 6:56 57	31/8/18 0:01 57
259/18 14:06 57 289/18 11:1 56 27/8/18 5:0 28/8/18 11:1 56 28/8/18 11:1 56 28/8/18 15:1 56 28/8/18 15:6 29/8/18 22:1 57 31/8/18 0:2 55 29/8/18 22:1 57 31/8/18 0:2 55 29/8/18 22:1 57 31/8/18 0:3 55 29/8/18 22:3 58 31/8/18 0:3 55 29/8/18 23:3 58 31/8/18 0:3 55 29/8/18 23:3 56 29/8/18 23:3 56 29/8/18 23:3 56 29/8/18 23:3 56 29/8/18 23:3 56 29/8/18 23:3 56 29/8/18 23:3 56 29/8/18 23:4 57 29/8/18 23:4 57 29/8/18 23:6 57 31/8/18 10:1 57 29/8/18 23:6 57 31/8/18 10:1 57 29/8/18 23:6 57						
259/18 14:16 56 28/0/18 2:32 57 31/0/18 0:26 58 259/18 14:26 60 26/0/18 1:33 54 27/0/18 5:6 28/0/18 2:33 58 31/0/18 0:36 57 259/18 1:33 26/0/18 1:36 53 28/0/18 5:3 28/0/18 5:3 28/0/18 5:3 28/0/18 5:3 28/0/18 5:3 28/0/18 5:3 28/0/18 5:3 28/0/18 5:4 28/0/18 5:6 28/0/18 5:6 28/0/18 5:6 28/0/18 5:6 28/0/18 5:6 5 29/0/18 23:5 57 31/0/18 0:51 55 28/0/18 5:6 5 28/0/18 0:15 57 30/0/18 0:16 56 28/0/18 0:16 57 30/0/18 0:16 56 31/0/18 1:10 56 25/0/18 1:11 56 25/0/18 1:11 56 25/0/18 1:11 55 26/0/	25/9/18 14:06 57	26/9/18 19:11 56	27/8/18 5:01 55	28/8/18 6:06 55	29/8/18 23:11 58	31/8/18 0:16 58
259/18 14.26 60 269/18 19:36 57 27/8/18 5:26 28/8/18 6:26 29/8/18 23:31 58 31/8/18 0:36 55 259/18 14:36 53 269/18 19:46 51 27/8/18 5:6 28/8/18 6:61 55 29/8/18 23:41 57 31/8/18 0:46 55 259/18 14:41 56 26/9/18 19:46 51 57 28/8/18 6:56 29/8/18 23:41 57 31/8/18 0:56 55 259/18 14:56 54 26/9/18 19:56 45 28/8/18 6:51 57 29/8/18 20:51 58 31/8/18 10:65 55 29/9/18 10:65 56 28/8/18 20:66 31/8/18 11:6 56 28/8/18 20:61 27/8/18 56 57 28/8/18 20:61 29 29/8/18 20:61 31/8/18 12:6 56 31/8/18 11:6 56						
259/18 14.31 5.3 269/18 19.36 57 27/8/18 5.31 56 28/8/18 6.31 57 31/8/18 14.41 56 29/8/18 23.46 58 31/8/18 15.5 29/8/18 12.46 58 31/8/18 56 28/8/18 6.41 55 29/8/18 23.46 58 31/8/18 10.51 56 25/9/18 14.46 58 29/8/18 6.46 56 29/8/18 6.56 57 29/8/18 6.56 57 29/8/18 6.56 57 29/8/18 6.56 57 29/8/18 6.56 57 29/8/18 6.56 57 29/8/18 6.56 57 29/8/18 6.56 57 29/8/18 20.11 53 31/8/18 11.11 56 25/9/18 15.16 56 29/9/18 16.56 57 29/8/18 20.11 49 27/8/18 6.56 57 30/8/18 20.16 55 31/8/18 11.1 56 25/9/18						
259/18 14:41 56 29/0/18 19:46 51 27/0/18 5:46 57 228/0/18 6:46 56 29/0/18 2:56 53 31/0/18 0:56 55 259/18 14:45 59 26/0/18 19:56 48 27/0/18 5:46 57 228/0/18 6:56 29/0/18 0:30 57 31/0/18 0:56 57 30/0/18 0:10 57 31/0/18 0:6 59 31/0/18 0:10 55 226/0/18 2:00 16 57 28/0/18 6:56 23/0/18 0:11 58 30/0/18 0:11 58 31/0/18 1:11 55 25/0/18 1:11 58 28/0/18 2:11 56 23/0/18 1:11 55 25/0/18 1:11 58 28/0/18 2:11 57 28/0/18 2:11 57 28/0/18 2:11 57 28/0/18 2:11 57 28/0/18 2:11 57 28/0/18 2:11 57 28/0/18 2:11 57 28/0/18 2:15 55 26/0/18 2:16 1:16	25/9/18 14:31 53	26/9/18 19:36 57	27/8/18 5:26 56	28/8/18 6:31 59	29/8/18 23:36 57	31/8/18 0:41 56
259/18 14:46 58 269/18 19:56 48 27/8/18 54 57 29/8/18 25.56 57 31/8/18 10:1 57 259/18 14:56 54 269/18 200/18 200/18 55:1 57 28/8/18 55:6 57 30/8/18 00:6 59 31/8/18 10:1 57 259/18 15:16 55 269/18 20:16 49 27/8/18 56 57 28/8/18 23:06 58 30/8/18 01:6 56 28/8/18 23:06 58 30/8/18 01:6 56 31/8/18 11:1 56 25/9/18 15:16 56 26/9/18 20:21 62 27/8/18 57 28/8/18 23:1 57 30/8/18 02:1 56 31/8/18 12:6 56 31/8/18 12:6 56 31/8/18 13:6 55 25/9/18 13:6 56 31/8/18 14:6 56 30/8/18 03:6 57 <						
259/18 15.6 54 26/9/18 20/0/18 20/0/18 25.7 28/8/18 55.6 57 30/8/18 0.01 57 31/8/18 10.6 56 25/9/18 15.06 55 26/9/18 20.11 49 27/8/18 56 57 28/8/18 23.00 58 30/8/18 0.01 56 31/8/18 11.1 56 25/9/18 15.16 56 28/9/18 20.7 28/8/18 23.01 58 30/8/18 0.01 57 31/8/18 11.1 56 25/9/18 15.21 56 26/9/18 20.21 57 30/8/18 0.21 56 31/8/18 13.1 55 25/9/18 15.31 55 26/9/18 20.31 57 30/8/18 23.6 57 30/8/18 0.30 57 31/8/18 14.1 56 25/9/18 15.31 55 26/9/18 20.36 61 27/8/18 6.31 57 30/8/18 0.31			27/8/18 5:41 59	28/8/18 6:46 56		31/8/18 0:56 56
259/18 15:06 55 28/9/18 20:11 49 27/8/18 6:01 56 28/8/18 23:06 58 30/8/18 0:11 58 31/8/18 1:12 56 25/9/18 15:16 56 26/9/18 20:21 62 27/8/18 6:06 56 28/8/18 23:11 59 30/8/18 0:16 56 31/8/18 1:21 56 25/9/18 15:16 56 26/9/18 20:21 62 27/8/18 6:16 57 28/8/18 23:21 57 30/8/18 0:26 56 31/8/18 1:26 56 25/9/18 15:36 55 26/9/18 20:31 59 27/8/18 6:21 57 28/8/18 23:36 57 30/8/18 0:41 56 31/8/18 1:46 58 25/9/18 15:36 55 26/9/18 20:44 61 27/8/18 6:31 57 28/8/18 23:46 56 30/8/18 0:41 56 31/8/18 1:46 58 25/9/18 15:46 54 26/9/18 20:46 61 27/8/18 6:51 58 28/8/18 23:46 56 30/8/18 0:46 55 31/8/18 2:01 55 25/9/18 16:01 56 26/9/18 21:06 53	25/9/18 14:56 54	26/9/18 20:01 62	27/8/18 5:51 57	28/8/18 6:56 57	30/8/18 0:01 57	31/8/18 1:06 56
25% 18 54 26% 18 30% 18 16 56 31% 18 12 56 25% 18 15.21 56 26% 18 21 56 31% 18 1.26 56 31% 18 1.26 56 31% 18 1.26 56 31% 18 1.3 55 25% 18 15.21 56 26% 18 2.71% 18 6.21 57 28% 18 2.331 57 30% 18 0.36 57 31% 18 1.41 56 25% 18 5.36 26% 18 2.331 57 30% 18 0.44 56 31% 18 1.46 58 28% 18 2.34 57 30% 18 0.44 56 31% 18 2.46 56 31% 18 2.46 56 31% 18 2.26 18 2.36						
259(18 15:21 56 269(18 20:26 54 27/8/18 6:16 57 28/8/18 23:26 57 30/8/18 0:26 56 31/8/18 1:31 55 25/9/18 15:31 55 26/9/18 20:36 62 27/8/18 6:26 57 28/8/18 23:26 57 30/8/18 0:36 57 31/8/18 1:41 56 25/9/18 15:36 55 26/9/18 20:41 62 27/8/18 6:26 57 28/8/18 23:36 57 30/8/18 0:41 56 31/8/18 1:46 58 25/9/18 15:46 54 26/9/18 20:51 61 27/8/18 6:46 58 28/8/18 23:46 56 30/8/18 0:46 55 31/8/18 1:56 55 25/9/18 15:56 51 26/9/18 21:06 53 27/8/18 6:51 58 28/8/18 23:51 56 30/8/18 0:65 56 31/8/18 2:11 55 25/9/18 16:56 51 26/9/18 21:16 52 27/8/18 6:51 58 28/8/18 23:51 56 30/8/18 1:01 56 31/8/18 2:11 55 25/9/18 16:06 57 26/9/18 21:16 52	25/9/18 15:11 54	26/9/18 20:16 49	27/8/18 6:06 56	28/8/18 23:11 58	30/8/18 0:16 56	31/8/18 1:21 56
25/9/18 15:31 55 26/9/18 20:36 62 27/8/18 6:26 57 28/8/18 23:31 57 30/8/18 0:36 57 31/8/18 1:41 56 25/9/18 15:41 57 26/9/18 20:41 62 27/8/18 6:36 58 28/8/18 23:36 57 30/8/18 0:41 56 31/8/18 1:51 56 25/9/18 15:41 57 26/9/18 20:51 61 27/8/18 6:46 58 28/8/18 23:46 56 30/8/18 0:41 55 31/8/18 1:51 55 25/9/18 15:56 51 26/9/18 21:01 62 27/8/18 6:51 58 28/8/18 23:56 57 30/8/18 1:06 56 31/8/18 2:06 56 25/9/18 16:01 56 26/9/18 21:01 62 27/8/18 6:51 58 28/8/18 23:56 57 30/8/18 1:06 56 31/8/18 2:01 55 25/9/18 16:06 57 26/9/18 21:01 62 27/8/18 2:30 61 29/8/18 0:01 58 30/8/18 1:16 56 31/8/18 2:1 57 25/9/18 16:11 58 26/9/18 21:21 61 27/8/18 23:21 58 29/8/18 0:11 59 30/8/18 1:21 55		26/9/18 20:26 54		28/8/18 23:21 57		
25/9/18 15:36 55 26/9/18 201/8 15:37 28/9/18 23:36 57 30/8/18 0:41 56 31/8/18 1:58 25/9/18 15:46 54 26/9/18 20:51 61 27/8/18 58 28/8/18 23:41 57 30/8/18 0:46 55 31/8/18 1:55 25/9/18 15:56 51 26/9/18 20:56 61 27/8/18 58 28/8/18 23:56 57 30/8/18 0:56 53 31/8/18 1:56 53 25/9/18 15:56 51 26/9/18 21:06 53 27/8/18 56 57 30/8/18 1:06 56 31/8/18 2:11 58 25/9/18 16:06 57 26/9/18 21:16 52 27/8/18 2:301 60 29/8/18 0:11 59 30/8/18 1:16 56 31/8/18 2:16 58 26/9/18 1:16 55 31/8/18 2:26 56 25/9/1						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	25/9/18 15:36 55	26/9/18 20:41 62	27/8/18 6:31 57	28/8/18 23:36 57	30/8/18 0:41 56	31/8/18 1:46 58
25/9/18 15:56 53 26/9/18 27/8/18 6:46 58 28/8/18 23:51 56 30/8/18 0:56 56 31/8/18 2:01 55 25/9/18 15:56 51 26/9/18 21:06 53 27/8/18 6:51 58 28/8/18 23:56 57 30/8/18 1:01 56 31/8/18 2:01 58 25/9/18 16:01 56 26/9/18 21:06 53 27/8/18 6:51 29/8/18 0:01 58 30/8/18 1:10 55 31/8/18 2:11 57 25/9/18 16:11 58 26/9/18 2:12 61 27/8/18 2:31 58 29/8/18 0:11 59 30/8/18 1:21 55 31/8/18 2:21 56 25/9/18 16:21 54 26/9/18 2:36 60 29/8/18 0:21 57 30/8/18 1:31 55 31/8/18 2:36 57 25/9/18 16:31						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	25/9/18 15:51 53	26/9/18 20:56 61	27/8/18 6:46 58	28/8/18 23:51 56	30/8/18 0:56 56	31/8/18 2:01 55
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	25/9/18 16:01 56	26/9/18 21:06 53	27/8/18 6:56 59	29/8/18 0:01 58	30/8/18 1:06 56	31/8/18 2:11 58
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						
25/9/18 16:26 55 26/9/18 21:31 61 27/8/18 23:21 58 29/8/18 0:26 57 30/8/18 1:31 55 31/8/18 2:36 57 25/9/18 16:31 54 26/9/18 21:36 49 27/8/18 2:3:26 60 29/8/18 0:31 57 30/8/18 1:36 56 31/8/18 2:46 56 25/9/18 16:41 53 26/9/18 21:41 55 27/8/18 2:3:31 64 29/8/18 0:31 57 30/8/18 1:46 54 31/8/18 2:46 56 25/9/18 16:46 55 26/9/18 2:14 61 29/8/18 0:46 60 30/8/18 1:46 54 31/8/18 2:51 55 25/9/18 16:56 45 26/9/18 2:16 61 27/8/18 2:3:51 57 29/8/18 0:56 58 30/8/18 2:01 55 31/8/18 3:06 55	25/9/18 16:16 58	26/9/18 21:21 61	27/8/18 23:11 59	29/8/18 0:16 58	30/8/18 1:21 55	31/8/18 2:26 56
25/9/18 16:31 54 26/9/18 21/8/18 23:26 60 29/8/18 157 30/8/18 1:36 56 31/8/18 2:41 56 25/9/18 16:36 58 26/9/18 1:41 55 27/8/18 2:331 64 29/8/18 59 30/8/18 1:41 55 31/8/18 2:46 56 25/9/18 16:41 53 26/9/18 2:16 61 27/8/18 2:3:1 64 29/8/18 0:36 59 30/8/18 1:46 54 31/8/18 2:46 56 25/9/18 16:41 53 26/9/18 2:1:6 61 27/8/18 2:3:41 61 29/8/18 0:51 57 30/8/18 1:56 54 31/8/18 2:56 54 25/9/18 16:51 52 26/9/18 2:156 58 29/8/18 0:51 57 30/8/18 2:06 53 31/8/18 3:11 55 25/9/18 17:01 58	25/9/18 16:26 55	26/9/18 21:31 61	27/8/18 23:21 58	29/8/18 0:26 57	30/8/18 1:31 55	31/8/18 2:36 57
25/9/18 16:41 53 26/9/18 21:46 62 27/8/18 23:36 57 29/8/18 0:41 59 30/8/18 1:46 54 31/8/18 2:51 55 25/9/18 16:46 55 26/9/18 21:6 61 27/8/18 23:34 61 29/8/18 0:46 60 30/8/18 1:55 31/8/18 2:56 54 25/9/18 16:51 52 26/9/18 21:56 61 27/8/18 2:51 57 29/8/18 0:56 58 30/8/18 1:56 54 31/8/18 3:06 55 25/9/18 16:56 43 27/8/18 2:51 57 29/8/18 1:56 58 30/8/18 2:01 55 31/8/18 3:06 55 25/9/18 17:01 58 26/9/18 2:01 53 31/8/18 3:16 56 25/9/18 17:06 61 26/9/18 2:11 61 28/8/18 0:06 56	25/9/18 16:31 54			29/8/18 0:31 57	30/8/18 1:36 56	31/8/18 2:41 56
25/9/18 16:51 52 26/9/18 21:56 61 27/8/18 23:46 57 29/8/18 0:51 57 30/8/18 1:56 54 31/8/18 3:01 55 25/9/18 16:56 45 26/9/18 22:01 62 27/8/18 23:51 57 29/8/18 0:56 58 30/8/18 1:56 54 31/8/18 3:01 55 25/9/18 17:01 58 26/9/18 22:06 43 27/8/18 23:56 58 29/8/18 1:01 57 30/8/18 2:06 55 31/8/18 3:01 55 25/9/18 17:06 61 26/9/18 22:11 61 28/8/18 0:01 59 29/8/18 1:06 57 30/8/18 2:16 53 31/8/18 3:11 56 25/9/18 17:11 61 28/8/18 0:01 59 29/8/18 1:11 55 30/8/18 2:16 53 31/8/18 3:16 56 25/9/18 17:16 52 26/9/18 22:12 61 28/8/18 0:01 59 29/8/18 1:11 55 30/8/18 2:16 53 31/8/18 3:21 57 25/9/18 17:16 52 26/9/18 22:26 61 28/8/18 0:11 56	25/9/18 16:41 53	26/9/18 21:46 62	27/8/18 23:36 57	29/8/18 0:41 59	30/8/18 1:46 54	31/8/18 2:51 55
25/9/18 16:56 45 26/9/18 22:01 62 27/8/18 23:51 57 29/8/18 0:56 58 30/8/18 2:01 55 31/8/18 3:06 55 25/9/18 17:01 58 26/9/18 22:06 43 27/8/18 23:56 58 29/8/18 1:01 57 30/8/18 2:06 55 31/8/18 3:06 55 25/9/18 17:01 61 26/9/18 22:11 61 28/8/18 0:01 59 29/8/18 1:06 57 30/8/18 2:11 55 31/8/18 3:16 56 25/9/18 17:16 61 28/8/18 0:06 56 29/8/18 1:11 55 30/8/18 2:16 53 31/8/18 3:16 57 25/9/18 17:16 52 26/9/18 22:21 61 28/8/18 0:16 57 29/8/18 1:16 55 30/8/18 2:16 53 31/8/18 3:26 56 25/9/18 17:21 56 26/9/18 22:26 61 28/8/18 0:16 57 29/8/18 1:21 55 30/8/18 2:26 54 31/8/18 3:31 57						
25/9/18 17:06 61 26/9/18 22:11 61 28/8/18 0:01 59 29/8/18 1:06 57 30/8/18 2:11 55 31/8/18 3:16 56 25/9/18 17:11 61 26/9/18 22:16 61 28/8/18 0:06 56 29/8/18 1:11 55 30/8/18 2:16 53 31/8/18 3:21 57 25/9/18 17:16 52 26/9/18 22:21 61 28/8/18 0:16 56 29/8/18 1:11 55 30/8/18 2:21 53 31/8/18 3:26 56 25/9/18 17:21 56 26/9/18 22:26 61 28/8/18 0:16 57 29/8/18 1:21 55 30/8/18 2:21 53 31/8/18 3:21 57 25/9/18 17:21 56 26/9/18 22:26 61 28/8/18 0:16 57 29/8/18 1:21 55 30/8/18 2:26 54 31/8/18 3:31 57	25/9/18 16:56 45	26/9/18 22:01 62	27/8/18 23:51 57	29/8/18 0:56 58	30/8/18 2:01 55	31/8/18 3:06 55
25/9/18 17:11 61 26/9/18 22:16 61 28/8/18 0:06 56 29/8/18 1:11 55 30/8/18 2:16 53 31/8/18 3:21 57 25/9/18 17:16 52 26/9/18 22:21 61 28/8/18 0:11 56 29/8/18 1:16 55 30/8/18 2:21 53 31/8/18 3:26 56 25/9/18 17:21 56 26/9/18 22:26 61 28/8/18 0:16 57 29/8/18 1:21 55 30/8/18 2:26 54 31/8/18 3:31 57	25/9/18 17:06 61	26/9/18 22:11 61	28/8/18 0:01 59	29/8/18 1:06 57	30/8/18 2:11 55	31/8/18 3:16 56
25/9/18 17:21 56 26/9/18 22:26 61 28/8/18 0:16 57 29/8/18 1:21 55 30/8/18 2:26 54 31/8/18 3:31 57		26/9/18 22:16 61 26/9/18 22:21 61				
20/8/10/17.20 30 20/8/18/231 51 20/8/18/021 56 29/8/18/125 56 30/8/18/231 54 31/8/18/336 56	25/9/18 17:21 56	26/9/18 22:26 61	28/8/18 0:16 57	29/8/18 1:21 55	30/8/18 2:26 54	31/8/18 3:31 57
	20/9/10 17:20 56	20/9/18 22:31 61	20/0/10 0:21 56	23/0/101:20 56	30/0/10 2:31 54	31/0/183:36 56

31/8/18 3:41 31/8/18 3:46	<u>9 Data</u> 56 55	RTN2a (Hong Kon 1/9/18 4:46 1/9/18 4:51	54 54 54	2/9/18 5:51 2/9/18 5:56	53 55	3/9/18 6:56 3/9/18 23:01	57 59	5/9/18 0:01 5/9/18 0:06	57 57	6/9/18 1:06 6/9/18 1:11	59 58
31/8/18 3:51	56	1/9/18 4:56	55	2/9/18 6:01	53	3/9/18 23:06	58	5/9/18 0:11	57	6/9/18 1:16	59
31/8/18 3:56 31/8/18 4:01	58 56	1/9/18 5:01 1/9/18 5:06	56 56	2/9/18 6:06 2/9/18 6:11	55 53	3/9/18 23:11 3/9/18 23:16	57 58	5/9/18 0:16 5/9/18 0:21	56 56	6/9/18 1:21 6/9/18 1:26	58 59
31/8/18 4:06	55	1/9/18 5:11	56	2/9/18 6:16	57	3/9/18 23:21	57	5/9/18 0:26	58	6/9/18 1:31	59
31/8/18 4:11	57	1/9/18 5:16	55	2/9/18 6:21	54	3/9/18 23:26	57	5/9/18 0:31	56	6/9/18 1:36	59
31/8/18 4:16	56	1/9/18 5:21	56 55	2/9/18 6:26	53 54	3/9/18 23:31	58 58	5/9/18 0:36	56 56	6/9/18 1:41	59
31/8/18 4:21 31/8/18 4:26	56 55	1/9/18 5:26 1/9/18 5:31	55	2/9/18 6:31 2/9/18 6:36	53	3/9/18 23:36 3/9/18 23:41	56	5/9/18 0:41 5/9/18 0:46	56	6/9/18 1:46 6/9/18 1:51	59 59
31/8/18 4:31	56	1/9/18 5:36	55	2/9/18 6:41	54	3/9/18 23:46	57	5/9/18 0:51	57	6/9/18 1:56	58
31/8/18 4:36	57	1/9/18 5:41	55 55	2/9/18 6:46	55	3/9/18 23:51	59	5/9/18 0:56	56	6/9/18 2:01	58
31/8/18 4:41 31/8/18 4:46	55 55	1/9/18 5:46 1/9/18 5:51	55 55	2/9/18 6:51 2/9/18 6:56	55 54	3/9/18 23:56 4/9/18 0:01	58 56	5/9/18 1:01 5/9/18 1:06	56 56	6/9/18 2:06 6/9/18 2:11	59 59
31/8/18 4:51	55	1/9/18 5:56	55	2/9/18 23:01	57	4/9/18 0:06	58	5/9/18 1:11	56	6/9/18 2:16	58
31/8/18 4:56	55 56	1/9/18 6:01	57 57	2/9/18 23:06 2/9/18 23:11	57 57	4/9/18 0:11 4/9/18 0:16	57	5/9/18 1:16 5/9/18 1:21	55 56	6/9/18 2:21 6/9/18 2:26	59 59
31/8/18 5:01 31/8/18 5:06	55	1/9/18 6:06 1/9/18 6:11	56	2/9/18 23:16	58	4/9/18 0:21	56 56	5/9/18 1:26	56	6/9/18 2:20	59
31/8/18 5:11	55	1/9/18 6:16	57	2/9/18 23:21	56	4/9/18 0:26	56	5/9/18 1:31	56	6/9/18 2:36	58
31/8/18 5:16	54 55	1/9/18 6:21	64	2/9/18 23:26	56	4/9/18 0:31	56	5/9/18 1:36	54 55	6/9/18 2:41	58
31/8/18 5:21 31/8/18 5:26	55 58	1/9/18 6:26 1/9/18 6:31	58 58	2/9/18 23:31 2/9/18 23:36	56 56	4/9/18 0:36 4/9/18 0:41	57 57	5/9/18 1:41 5/9/18 1:46	55 56	6/9/18 2:46 6/9/18 2:51	58 59
31/8/18 5:31	55	1/9/18 6:36	56	2/9/18 23:41	56	4/9/18 0:46	56	5/9/18 1:51	57	6/9/18 2:56	58
31/8/18 5:36	55	1/9/18 6:41	57	2/9/18 23:46	55	4/9/18 0:51	56	5/9/18 1:56	55 54	6/9/18 3:01	58
31/8/18 5:41 31/8/18 5:46	55 56	1/9/18 6:46 1/9/18 6:51	56 57	2/9/18 23:51 2/9/18 23:56	59 57	4/9/18 0:56 4/9/18 1:01	56 55	5/9/18 2:01 5/9/18 2:06	54 55	6/9/18 3:06 6/9/18 3:11	58 59
31/8/18 5:51	56	1/9/18 6:56	56	3/9/18 0:01	55	4/9/18 1:06	55	5/9/18 2:11	55	6/9/18 3:16	58
31/8/18 5:56 31/8/18 6:01	56 56	1/9/18 23:01 1/9/18 23:06	56 55	3/9/18 0:06 3/9/18 0:11	59 55	4/9/18 1:11 4/9/18 1:16	55 55	5/9/18 2:16 5/9/18 2:21	56 55	6/9/18 3:21 6/9/18 3:26	58 57
31/8/18 6:06	57	1/9/18 23:11	57	3/9/18 0:16	55	4/9/18 1:21	55	5/9/18 2:26	55	6/9/18 3:20	58
31/8/18 6:11	57	1/9/18 23:16	55	3/9/18 0:21	55	4/9/18 1:26	55	5/9/18 2:31	55	6/9/18 3:36	59
31/8/18 6:16 31/8/18 6:21	56 56	1/9/18 23:21 1/9/18 23:26	56 54	3/9/18 0:26 3/9/18 0:31	56 55	4/9/18 1:31 4/9/18 1:36	56 56	5/9/18 2:36 5/9/18 2:41	55 54	6/9/18 3:41 6/9/18 3:46	58 58
31/8/18 6:26	56	1/9/18 23:31	55	3/9/18 0:36	55	4/9/18 1:41	55	5/9/18 2:46	54	6/9/18 3:51	58
31/8/18 6:31	58	1/9/18 23:36	55	3/9/18 0:41	57	4/9/18 1:46	55	5/9/18 2:51	54	6/9/18 3:56	58
31/8/18 6:36 31/8/18 6:41	58 57	1/9/18 23:41 1/9/18 23:46	58 55	3/9/18 0:46 3/9/18 0:51	55 55	4/9/18 1:51 4/9/18 1:56	54 54	5/9/18 2:56 5/9/18 3:01	54 54	6/9/18 4:01 6/9/18 4:06	58 57
31/8/18 6:46	58	1/9/18 23:51	56	3/9/18 0:56	55	4/9/18 2:01	54	5/9/18 3:06	53	6/9/18 4:11	56
31/8/18 6:51	58	1/9/18 23:56	54	3/9/18 1:01	55	4/9/18 2:06	54	5/9/18 3:11	54	6/9/18 4:16	56
31/8/18 6:56 31/8/18 23:01	58 58	2/9/18 0:01 2/9/18 0:06	55 59	3/9/18 1:06 3/9/18 1:11	55 56	4/9/18 2:11 4/9/18 2:16	55 54	5/9/18 3:16 5/9/18 3:21	55 55	6/9/18 4:21 6/9/18 4:26	56 57
31/8/18 23:06	57	2/9/18 0:11	55	3/9/18 1:16	54	4/9/18 2:21	54	5/9/18 3:26	54	6/9/18 4:31	58
31/8/18 23:11	59	2/9/18 0:16	55	3/9/18 1:21	56	4/9/18 2:26	53	5/9/18 3:31	53	6/9/18 4:36	59
31/8/18 23:16 31/8/18 23:21	57 57	2/9/18 0:21 2/9/18 0:26	56 54	3/9/18 1:26 3/9/18 1:31	54 54	4/9/18 2:31 4/9/18 2:36	53 54	5/9/18 3:36 5/9/18 3:41	54 54	6/9/18 4:41 6/9/18 4:46	58 58
31/8/18 23:26	57	2/9/18 0:31	55	3/9/18 1:36	54	4/9/18 2:41	54	5/9/18 3:46	54	6/9/18 4:51	57
31/8/18 23:31	58	2/9/18 0:36	54	3/9/18 1:41	54	4/9/18 2:46	53	5/9/18 3:51	53	6/9/18 4:56	57
31/8/18 23:36 31/8/18 23:41	57 57	2/9/18 0:41 2/9/18 0:46	54 59	3/9/18 1:46 3/9/18 1:51	55 54	4/9/18 2:51 4/9/18 2:56	53 54	5/9/18 3:56 5/9/18 4:01	54 54	6/9/18 5:01 6/9/18 5:06	57 58
31/8/18 23:46	57	2/9/18 0:51	57	3/9/18 1:56	54	4/9/18 3:01	53	5/9/18 4:06	54	6/9/18 5:11	58
31/8/18 23:51 31/8/18 23:56	56 57	2/9/18 0:56 2/9/18 1:01	55 53	3/9/18 2:01 3/9/18 2:06	52 54	4/9/18 3:06 4/9/18 3:11	54 53	5/9/18 4:11 5/9/18 4:16	54 55	6/9/18 5:16 6/9/18 5:21	57 58
1/9/18 0:01	57	2/9/18 1:06	53	3/9/18 2:11	55	4/9/18 3:16	58	5/9/18 4:21	53	6/9/18 5:26	58 59
1/9/18 0:06	57	2/9/18 1:11	54	3/9/18 2:16	52	4/9/18 3:21	54	5/9/18 4:26	54	6/9/18 5:31	59
1/9/18 0:11 1/9/18 0:16	60 57	2/9/18 1:16 2/9/18 1:21	55 52	3/9/18 2:21 3/9/18 2:26	53 54	4/9/18 3:26 4/9/18 3:31	53 54	5/9/18 4:31 5/9/18 4:36	53 52	6/9/18 5:36 6/9/18 5:41	57 58
1/9/18 0:21	57	2/9/18 1:26	53	3/9/18 2:31	53	4/9/18 3:36	54	5/9/18 4:41	53	6/9/18 5:46	58
1/9/18 0:26	57	2/9/18 1:31	53	3/9/18 2:36	53	4/9/18 3:41	55	5/9/18 4:46	54	6/9/18 5:51	58
1/9/18 0:31 1/9/18 0:36	57 57	2/9/18 1:36 2/9/18 1:41	56 54	3/9/18 2:41 3/9/18 2:46	55 53	4/9/18 3:46 4/9/18 3:51	54 54	5/9/18 4:51 5/9/18 4:56	55 55	6/9/18 5:56 6/9/18 6:01	58 58
1/9/18 0:41	57	2/9/18 1:46	52	3/9/18 2:51	54	4/9/18 3:56	54	5/9/18 5:01	54	6/9/18 6:06	59
1/9/18 0:46	57	2/9/18 1:51	54	3/9/18 2:56	51	4/9/18 4:01	56	5/9/18 5:06	54	6/9/18 6:11	60
1/9/18 0:51 1/9/18 0:56	57 57	2/9/18 1:56 2/9/18 2:01	54 54	3/9/18 3:01 3/9/18 3:06	54 54	4/9/18 4:06 4/9/18 4:11	54 54	5/9/18 5:11 5/9/18 5:16	54 54	6/9/18 6:16 6/9/18 6:21	59 59
1/9/18 1:01	58	2/9/18 2:06	55	3/9/18 3:11	52	4/9/18 4:16	55	5/9/18 5:21	54	6/9/18 6:26	59
1/9/18 1:06	57 57	2/9/18 2:11 2/9/18 2:16	54	3/9/18 3:16 3/9/18 3:21	54 54	4/9/18 4:21	56	5/9/18 5:26	54 55	6/9/18 6:31	59
1/9/18 1:11 1/9/18 1:16	58	2/9/18 2:21	52 53	3/9/18 3:26	55	4/9/18 4:26 4/9/18 4:31	55 54	5/9/18 5:31 5/9/18 5:36	55 54	6/9/18 6:36 6/9/18 6:41	59 59
1/9/18 1:21	57	2/9/18 2:26	53	3/9/18 3:31	54	4/9/18 4:36	54	5/9/18 5:41	55	6/9/18 6:46	59
1/9/18 1:26 1/9/18 1:31	56 56	2/9/18 2:31 2/9/18 2:36	53 54	3/9/18 3:36 3/9/18 3:41	52 52	4/9/18 4:41 4/9/18 4:46	53 54	5/9/18 5:46 5/9/18 5:51	55	6/9/18 6:51 6/9/18 6:56	60
1/9/18 1:36	56	2/9/18 2:41	53	3/9/18 3:46	52	4/9/18 4:51	54 54	5/9/18 5:56	55 55	6/9/18 23:01	60 60
1/9/18 1:41	56	2/9/18 2:46	53	3/9/18 3:51	51	4/9/18 4:56	54	5/9/18 6:01	56	6/9/18 23:06	60
1/9/18 1:46 1/9/18 1:51	56 56	2/9/18 2:51 2/9/18 2:56	52 54	3/9/18 3:56 3/9/18 4:01	51 52	4/9/18 5:01 4/9/18 5:06	55 54	5/9/18 6:06 5/9/18 6:11	56 56	6/9/18 23:11 6/9/18 23:16	59 60
1/9/18 1:56	56	2/9/18 3:01	53	3/9/18 4:06	52	4/9/18 5:11	53	5/9/18 6:16	58	6/9/18 23:21	59
1/9/18 2:01	56	2/9/18 3:06	53	3/9/18 4:11	51	4/9/18 5:16	54	5/9/18 6:21	59	6/9/18 23:26	58
1/9/18 2:06 1/9/18 2:11	56 57	2/9/18 3:11 2/9/18 3:16	51 52	3/9/18 4:16 3/9/18 4:21	52 53	4/9/18 5:21 4/9/18 5:26	56 54	5/9/18 6:26 5/9/18 6:31	57 57	6/9/18 23:31 6/9/18 23:36	57 58
1/9/18 2:16	57	2/9/18 3:21	51	3/9/18 4:26	52	4/9/18 5:31	53	5/9/18 6:36	56	6/9/18 23:41	59
1/9/18 2:21	56 57	2/9/18 3:26	50	3/9/18 4:31	51	4/9/18 5:36	57	5/9/18 6:41	58	6/9/18 23:46	58
1/9/18 2:26 1/9/18 2:31	57 56	2/9/18 3:31 2/9/18 3:36	50 52	3/9/18 4:36 3/9/18 4:41	52 50	4/9/18 5:41 4/9/18 5:46	55 56	5/9/18 6:46 5/9/18 6:51	59 58	6/9/18 23:51 6/9/18 23:56	57 58
1/9/18 2:36	56	2/9/18 3:41	51	3/9/18 4:46	53	4/9/18 5:51	56	5/9/18 6:56	57	7/9/18 0:01	59
1/9/18 2:41	56	2/9/18 3:46	51 52	3/9/18 4:51	52 52	4/9/18 5:56	56 56	5/9/18 23:01	60	7/9/18 0:06	59
1/9/18 2:46 1/9/18 2:51	56 56	2/9/18 3:51 2/9/18 3:56	52 51	3/9/18 4:56 3/9/18 5:01	52 52	4/9/18 6:01 4/9/18 6:06	56 56	5/9/18 23:06 5/9/18 23:11	60 59	7/9/18 0:11 7/9/18 0:16	58 57
1/9/18 2:56	55	2/9/18 4:01	51	3/9/18 5:06	58	4/9/18 6:11	55	5/9/18 23:16	60	7/9/18 0:21	57
1/9/18 3:01 1/9/18 3:06	57 63	2/9/18 4:06 2/9/18 4:11	51 53	3/9/18 5:11 3/9/18 5:16	54 53	4/9/18 6:16 4/9/18 6:21	56 57	5/9/18 23:21 5/9/18 23:26	60 60	7/9/18 0:26 7/9/18 0:31	59 58
1/9/18 3:06	63 57	2/9/18 4:11 2/9/18 4:16	53 52	3/9/18 5:16	53 54	4/9/18 6:26	57	5/9/18 23:26	60 60	7/9/18 0:31	58 56
1/9/18 3:16	55	2/9/18 4:21	52	3/9/18 5:26	53	4/9/18 6:31	56	5/9/18 23:36	61	7/9/18 0:41	55
1/9/18 3:21 1/9/18 3:26	55 55	2/9/18 4:26 2/9/18 4:31	54 51	3/9/18 5:31 3/9/18 5:36	53 53	4/9/18 6:36 4/9/18 6:41	56 57	5/9/18 23:41 5/9/18 23:46	60 60	7/9/18 0:46 7/9/18 0:51	56 57
1/9/18 3:26	55	2/9/18 4:31	51	3/9/18 5:36	53	4/9/18 6:46	57	5/9/18 23:51	61	7/9/18 0:56	57 57
1/9/18 3:36	54	2/9/18 4:41	52	3/9/18 5:46	53	4/9/18 6:51	58	5/9/18 23:56	59	7/9/18 1:01	56
1/9/18 3:41 1/9/18 3:46	54 55	2/9/18 4:46 2/9/18 4:51	53 50	3/9/18 5:51 3/9/18 5:56	53 53	4/9/18 6:56 4/9/18 23:01	58 58	6/9/18 0:01 6/9/18 0:06	60 60	7/9/18 1:06 7/9/18 1:11	57 56
1/9/18 3:51	55	2/9/18 4:56	50 50	3/9/18 6:01	53	4/9/18 23:01	58	6/9/18 0:08	60	7/9/18 1:16	57
1/9/18 3:56	55	2/9/18 5:01	52	3/9/18 6:06	55	4/9/18 23:11	57	6/9/18 0:16	59	7/9/18 1:21	57
1/9/18 4:01 1/9/18 4:06	54 55	2/9/18 5:06 2/9/18 5:11	52 52	3/9/18 6:11 3/9/18 6:16	56 55	4/9/18 23:16 4/9/18 23:21	58 57	6/9/18 0:21 6/9/18 0:26	59 59	7/9/18 1:26 7/9/18 1:31	56 55
1/9/18 4:06	55 54	2/9/18 5:11 2/9/18 5:16	52 54	3/9/18 6:16	55 55	4/9/18 23:21 4/9/18 23:26	57 58	6/9/18 0:26	59 59	7/9/18 1:31	55 56
1/9/18 4:16	55	2/9/18 5:21	54	3/9/18 6:26	57	4/9/18 23:31	58	6/9/18 0:36	59	7/9/18 1:41	55
1/9/18 4:21 1/9/18 4:26	54 55	2/9/18 5:26 2/9/18 5:31	54 52	3/9/18 6:31 3/9/18 6:36	56 59	4/9/18 23:36 4/9/18 23:41	59 59	6/9/18 0:41 6/9/18 0:46	60 59	7/9/18 1:46 7/9/18 1:51	55 54
1/9/18 4:26	55 55	2/9/18 5:36	52 52	3/9/18 6:36 3/9/18 6:41	59 58	4/9/18 23:46	59 57	6/9/18 0:46 6/9/18 0:51	59 60	7/9/18 1:51	54 55
	55	2/9/18 5:41	51	3/9/18 6:46	57	4/9/18 23:51	58	6/9/18 0:56	59	7/9/18 2:01	55
1/9/18 4:36 1/9/18 4:41	55	2/9/18 5:46	51	3/9/18 6:51	56	4/9/18 23:56	57	6/9/18 1:01	59	7/9/18 2:06	56

7/9/18 2:11 7/9/18 2:16	<u>e Data</u> 57 56	RTN2a (Hong Kor 8/9/18 3:16 8/9/18 3:21	55 55	9/9/18 4:21 9/9/18 4:26	44 42	10/9/18 5:26 51 10/9/18 5:31 49	11/9/18 6:31 56 11/9/18 6:36 56	12/9/18 23:36 46 12/9/18 23:41 58
7/9/18 2:21	56	8/9/18 3:26	55	9/9/18 4:31	45	10/9/18 5:36 48	11/9/18 6:41 57	12/9/18 23:46 58
7/9/18 2:26 7/9/18 2:31	56 55	8/9/18 3:31 8/9/18 3:36	56 55	9/9/18 4:36 9/9/18 4:41	48 39	10/9/18 5:41 50 10/9/18 5:46 51	11/9/18 6:46 56 11/9/18 6:51 57	12/9/18 23:51 58 12/9/18 23:56 58
7/9/18 2:36	56	8/9/18 3:41	56	9/9/18 4:46	43	10/9/18 5:51 50	11/9/18 6:56 56	13/9/18 0:01 58
7/9/18 2:41 7/9/18 2:46	55 55	8/9/18 3:46 8/9/18 3:51	56 56	9/9/18 4:51 9/9/18 4:56	42 52	10/9/18 5:56 51 10/9/18 6:01 49	11/9/18 23:01 55 11/9/18 23:06 54	13/9/18 0:06 58 13/9/18 0:11 58
7/9/18 2:51	56	8/9/18 3:56	56	9/9/18 5:01	45	10/9/18 6:06 50	11/9/18 23:06 54	13/9/18 0:16 58
7/9/18 2:56	54	8/9/18 4:01	56	9/9/18 5:06	45	10/9/18 6:11 53	11/9/18 23:16 58	13/9/18 0:21 57
7/9/18 3:01 7/9/18 3:06	54 54	8/9/18 4:06 8/9/18 4:11	55 54	9/9/18 5:11 9/9/18 5:16	56 58	10/9/18 6:16 52 10/9/18 6:21 53	11/9/18 23:21 55 11/9/18 23:26 56	13/9/18 0:26 58 13/9/18 0:31 57
7/9/18 3:11	54	8/9/18 4:16	55	9/9/18 5:21	44	10/9/18 6:26 54	11/9/18 23:31 56	13/9/18 0:36 57
7/9/18 3:16 7/9/18 3:21	58 56	8/9/18 4:21 8/9/18 4:26	55 54	9/9/18 5:26 9/9/18 5:31	45 46	10/9/18 6:31 52 10/9/18 6:36 53	11/9/18 23:36 56 11/9/18 23:41 57	13/9/18 0:41 57 13/9/18 0:46 57
7/9/18 3:26	54	8/9/18 4:31	54	9/9/18 5:36	46	10/9/18 6:41 53	11/9/18 23:46 56	13/9/18 0:51 57
7/9/18 3:31 7/9/18 3:36	58 55	8/9/18 4:36 8/9/18 4:41	54	9/9/18 5:41 9/9/18 5:46	40 44	10/9/18 6:46 54 10/9/18 6:51 55	11/9/18 23:51 56 11/9/18 23:56 58	13/9/18 0:56 57 13/9/18 1:01 57
7/9/18 3:41	53	8/9/18 4:46	55 56	9/9/18 5:51	44 45	10/9/18 6:56 55	12/9/18 0:01 56	13/9/18 1:06 58
7/9/18 3:46	52	8/9/18 4:51	55	9/9/18 5:56	46	10/9/18 23:01 58	12/9/18 0:06 56	13/9/18 1:11 58
7/9/18 3:51 7/9/18 3:56	52 55	8/9/18 4:56 8/9/18 5:01	54 55	9/9/18 6:01 9/9/18 6:06	50 44	10/9/18 23:06 56 10/9/18 23:11 59	12/9/18 0:11 55 12/9/18 0:16 55	13/9/18 1:16 57 13/9/18 1:21 57
7/9/18 4:01	57	8/9/18 5:06	55	9/9/18 6:11	50	10/9/18 23:16 57	12/9/18 0:21 58	13/9/18 1:26 57
7/9/18 4:06 7/9/18 4:11	54 53	8/9/18 5:11 8/9/18 5:16	55 55	9/9/18 6:16 9/9/18 6:21	48 60	10/9/18 23:21 56 10/9/18 23:26 57	12/9/18 0:26 57 12/9/18 0:31 57	13/9/18 1:31 57 13/9/18 1:36 57
7/9/18 4:16	53	8/9/18 5:21	55	9/9/18 6:26	54	10/9/18 23:31 59	12/9/18 0:36 56	13/9/18 1:41 56
7/9/18 4:21	53	8/9/18 5:26	55	9/9/18 6:31	48	10/9/18 23:36 56	12/9/18 0:41 55	13/9/18 1:46 56
7/9/18 4:26 7/9/18 4:31	53 52	8/9/18 5:31 8/9/18 5:36	55 54	9/9/18 6:36 9/9/18 6:41	53 51	10/9/18 23:41 56 10/9/18 23:46 56	12/9/18 0:46 61 12/9/18 0:51 55	13/9/18 1:51 57 13/9/18 1:56 56
7/9/18 4:36	52	8/9/18 5:41	54	9/9/18 6:46	51	10/9/18 23:51 55	12/9/18 0:56 56	13/9/18 2:01 56
7/9/18 4:41 7/9/18 4:46	53 56	8/9/18 5:46 8/9/18 5:51	55 56	9/9/18 6:51 9/9/18 6:56	52 52	10/9/18 23:56 56 11/9/18 0:01 56	12/9/18 1:01 55 12/9/18 1:06 56	13/9/18 2:06 57 13/9/18 2:11 57
7/9/18 4:51	55	8/9/18 5:56	55	9/9/18 23:01	56	11/9/18 0:06 56	12/9/18 1:11 56	13/9/18 2:16 57
7/9/18 4:56 7/9/18 5:01	53 54	8/9/18 6:01 8/9/18 6:06	56 56	9/9/18 23:06 9/9/18 23:11	56 56	11/9/18 0:11 55 11/9/18 0:16 56	12/9/18 1:16 54 12/9/18 1:21 54	13/9/18 2:21 57 13/9/18 2:26 57
7/9/18 5:06	54 54	8/9/18 6:11	56	9/9/18 23:16	57	11/9/18 0:21 56	12/9/18 1:26 58	13/9/18 2:31 57
7/9/18 5:11	54	8/9/18 6:16	56	9/9/18 23:21	59	11/9/18 0:26 56	12/9/18 1:31 56	13/9/18 2:36 57
7/9/18 5:16 7/9/18 5:21	54 55	8/9/18 6:21 8/9/18 6:26	57 55	9/9/18 23:26 9/9/18 23:31	58 60	11/9/18 0:31 55 11/9/18 0:36 55	12/9/18 1:36 55 12/9/18 1:41 56	13/9/18 2:41 56 13/9/18 2:46 56
7/9/18 5:26	54	8/9/18 6:31	58	9/9/18 23:36	58	11/9/18 0:41 55	12/9/18 1:46 54	13/9/18 2:51 56
7/9/18 5:31 7/9/18 5:36	55 55	8/9/18 6:36 8/9/18 6:41	56 57	9/9/18 23:41 9/9/18 23:46	57 65	11/9/18 0:46 55 11/9/18 0:51 55	12/9/18 1:51 54 12/9/18 1:56 54	13/9/18 2:56 56 13/9/18 3:01 57
7/9/18 5:41	55	8/9/18 6:46	57	9/9/18 23:51	56	11/9/18 0:56 54	12/9/18 2:01 54	13/9/18 3:06 56
7/9/18 5:46 7/9/18 5:51	55 56	8/9/18 6:51 8/9/18 6:56	58 58	9/9/18 23:56 10/9/18 0:01	57 55	11/9/18 1:01 54 11/9/18 1:06 54	12/9/18 2:06 54 12/9/18 2:11 53	13/9/18 3:11 56 13/9/18 3:16 56
7/9/18 5:56	55	8/9/18 23:01	58	10/9/18 0:06	54	11/9/18 1:11 54	12/9/18 2:16 54	13/9/18 3:21 56
7/9/18 6:01 7/9/18 6:06	56 57	8/9/18 23:06 8/9/18 23:11	56 56	10/9/18 0:11 10/9/18 0:16	53 57	11/9/18 1:16 54 11/9/18 1:21 55	12/9/18 2:21 55 12/9/18 2:26 54	13/9/18 3:26 56 13/9/18 3:31 56
7/9/18 6:11	55	8/9/18 23:16	56	10/9/18 0:21	54	11/9/18 1:26 54	12/9/18 2:31 54	13/9/18 3:36 56
7/9/18 6:16	56	8/9/18 23:21	56	10/9/18 0:26	54	11/9/18 1:31 57	12/9/18 2:36 52	13/9/18 3:41 56
7/9/18 6:21 7/9/18 6:26	56 56	8/9/18 23:26 8/9/18 23:31	56 55	10/9/18 0:31 10/9/18 0:36	53 53	11/9/18 1:36 53 11/9/18 1:41 53	12/9/18 2:41 53 12/9/18 2:46 52	13/9/18 3:46 56 13/9/18 3:51 56
7/9/18 6:31	56	8/9/18 23:36	55	10/9/18 0:41	51	11/9/18 1:46 52	12/9/18 2:51 53	13/9/18 3:56 56
7/9/18 6:36 7/9/18 6:41	56 57	8/9/18 23:41 8/9/18 23:46	54 54	10/9/18 0:46 10/9/18 0:51	53 60	11/9/18 1:51 55 11/9/18 1:56 54	12/9/18 2:56 52 12/9/18 3:01 53	13/9/18 4:01 56 13/9/18 4:06 56
7/9/18 6:46	57	8/9/18 23:51	57	10/9/18 0:56	52	11/9/18 2:01 52	12/9/18 3:06 54	13/9/18 4:11 56
7/9/18 6:51 7/9/18 6:56	57 57	8/9/18 23:56 9/9/18 0:01	56 54	10/9/18 1:01 10/9/18 1:06	52 50	11/9/18 2:06 53 11/9/18 2:11 54	12/9/18 3:11 54 12/9/18 3:16 54	13/9/18 4:16 56 13/9/18 4:21 56
7/9/18 23:01	58	9/9/18 0:06	54	10/9/18 1:11	52	11/9/18 2:16 53	12/9/18 3:21 53	13/9/18 4:26 57
7/9/18 23:06 7/9/18 23:11	59 59	9/9/18 0:11 9/9/18 0:16	53 53	10/9/18 1:16 10/9/18 1:21	48 47	11/9/18 2:21 56 11/9/18 2:26 53	12/9/18 3:26 53 12/9/18 3:31 53	13/9/18 4:31 56 13/9/18 4:36 56
7/9/18 23:16	57	9/9/18 0:21	54	10/9/18 1:26	43	11/9/18 2:31 52	12/9/18 3:36 52	13/9/18 4:41 56
7/9/18 23:21	58 57	9/9/18 0:26	53	10/9/18 1:31	48	11/9/18 2:36 52	12/9/18 3:41 55 12/9/18 3:46 53	13/9/18 4:46 56
7/9/18 23:26 7/9/18 23:31	57 61	9/9/18 0:31 9/9/18 0:36	53 53	10/9/18 1:36 10/9/18 1:41	46 46	11/9/18 2:41 52 11/9/18 2:46 52	12/9/18 3:46 53 12/9/18 3:51 55	13/9/18 4:51 56 13/9/18 4:56 56
7/9/18 23:36	59	9/9/18 0:41	54	10/9/18 1:46	48	11/9/18 2:51 54	12/9/18 3:56 53	13/9/18 5:01 56
7/9/18 23:41 7/9/18 23:46	57 57	9/9/18 0:46 9/9/18 0:51	53 53	10/9/18 1:51 10/9/18 1:56	50 48	11/9/18 2:56 52 11/9/18 3:01 51	12/9/18 4:01 53 12/9/18 4:06 53	13/9/18 5:06 56 13/9/18 5:11 56
7/9/18 23:51	57	9/9/18 0:56	53	10/9/18 2:01	48	11/9/18 3:06 52	12/9/18 4:11 53	13/9/18 5:16 57
7/9/18 23:56 8/9/18 0:01	58 57	9/9/18 1:01 9/9/18 1:06	53 53	10/9/18 2:06 10/9/18 2:11	48 45	11/9/18 3:11 52 11/9/18 3:16 51	12/9/18 4:16 53 12/9/18 4:21 53	13/9/18 5:21 56 13/9/18 5:26 56
8/9/18 0:06	57	9/9/18 1:11	54	10/9/18 2:16	44	11/9/18 3:21 52	12/9/18 4:26 52	13/9/18 5:31 56
8/9/18 0:11 8/9/18 0:16	58 59	9/9/18 1:16 9/9/18 1:21	52 52	10/9/18 2:21 10/9/18 2:26	49 46	11/9/18 3:26 52 11/9/18 3:31 53	12/9/18 4:31 52 12/9/18 4:36 53	13/9/18 5:36 56 13/9/18 5:41 56
8/9/18 0:21	57	9/9/18 1:26	52	10/9/18 2:31	48	11/9/18 3:36 53	12/9/18 4:41 54	13/9/18 5:46 56
8/9/18 0:26 8/9/18 0:31	57 56	9/9/18 1:31 9/9/18 1:36	52 53	10/9/18 2:36 10/9/18 2:41	47 43	11/9/18 3:41 52 11/9/18 3:46 52	12/9/18 4:46 55 12/9/18 4:51 56	13/9/18 5:51 56 13/9/18 5:56 56
8/9/18 0:36	57	9/9/18 1:41	51	10/9/18 2:41	43	11/9/18 3:51 50	12/9/18 4:56 54	13/9/18 5:56 56 13/9/18 6:01 57
8/9/18 0:41	59	9/9/18 1:46	50	10/9/18 2:51	47	11/9/18 3:56 52	12/9/18 5:01 53 12/9/18 5:06 53	13/9/18 6:06 57 13/9/18 6:11 58
8/9/18 0:46 8/9/18 0:51	59 58	9/9/18 1:51 9/9/18 1:56	50 52	10/9/18 2:56 10/9/18 3:01	45 32	11/9/18 4:01 52 11/9/18 4:06 52	12/9/18 5:06 53 12/9/18 5:11 53	13/9/18 6:11 58 13/9/18 6:16 57
8/9/18 0:56	57	9/9/18 2:01	52	10/9/18 3:06	43	11/9/18 4:11 53	12/9/18 5:16 53	13/9/18 6:21 57
8/9/18 1:01 8/9/18 1:06	58 57	9/9/18 2:06 9/9/18 2:11	51 50	10/9/18 3:11 10/9/18 3:16	42 45	11/9/18 4:16 53 11/9/18 4:21 53	12/9/18 5:21 53 12/9/18 5:26 54	13/9/18 6:26 58 13/9/18 6:31 58
8/9/18 1:11	57	9/9/18 2:16	48	10/9/18 3:21	51	11/9/18 4:26 53	12/9/18 5:31 53	13/9/18 6:36 58
8/9/18 1:16 8/9/18 1:21	55 56	9/9/18 2:21 9/9/18 2:26	48 49	10/9/18 3:26 10/9/18 3:31	50 47	11/9/18 4:31 53 11/9/18 4:36 54	12/9/18 5:36 52 12/9/18 5:41 52	13/9/18 6:41 58 13/9/18 6:46 50
8/9/18 1:26	58	9/9/18 2:31	49	10/9/18 3:36	50	11/9/18 4:41 54	12/9/18 5:46 53	13/9/18 6:51 44
8/9/18 1:31 8/9/18 1:36	58 58	9/9/18 2:36 9/9/18 2:41	48 48	10/9/18 3:41 10/9/18 3:46	48 47	11/9/18 4:46 53 11/9/18 4:51 53	12/9/18 5:51 54 12/9/18 5:56 53	13/9/18 6:56 58 13/9/18 23:01 56
8/9/18 1:41	57	9/9/18 2:46	40	10/9/18 3:51	39	11/9/18 4:56 54	12/9/18 6:01 54	13/9/18 23:06 50
8/9/18 1:46	55	9/9/18 2:51	56	10/9/18 3:56	58	11/9/18 5:01 53	12/9/18 6:06 54	13/9/18 23:11 47
8/9/18 1:51 8/9/18 1:56	57 56	9/9/18 2:56 9/9/18 3:01	49 52	10/9/18 4:01 10/9/18 4:06	45 40	11/9/18 5:06 53 11/9/18 5:11 52	12/9/18 6:11 55 12/9/18 6:16 55	13/9/18 23:16 47 13/9/18 23:21 58
8/9/18 2:01	56	9/9/18 3:06	51	10/9/18 4:11	44	11/9/18 5:16 53	12/9/18 6:21 55	13/9/18 23:26 58
8/9/18 2:06 8/9/18 2:11	56 56	9/9/18 3:11 9/9/18 3:16	52 52	10/9/18 4:16 10/9/18 4:21	46 43	11/9/18 5:21 53 11/9/18 5:26 54	12/9/18 6:26 55 12/9/18 6:31 57	13/9/18 23:31 48 13/9/18 23:36 46
8/9/18 2:16	56	9/9/18 3:21	54	10/9/18 4:26	46	11/9/18 5:31 53	12/9/18 6:36 56	13/9/18 23:41 58
8/9/18 2:21 8/9/18 2:26	58 58	9/9/18 3:26 9/9/18 3:31	56 53	10/9/18 4:31 10/9/18 4:36	47 46	11/9/18 5:36 54 11/9/18 5:41 54	12/9/18 6:41 57 12/9/18 6:46 57	13/9/18 23:46 58 13/9/18 23:51 58
8/9/18 2:31	56	9/9/18 3:36	54	10/9/18 4:41	45	11/9/18 5:46 54	12/9/18 6:51 57	13/9/18 23:56 42
8/9/18 2:36 8/9/18 2:41	56 56	9/9/18 3:41 9/9/18 3:46	53 54	10/9/18 4:46 10/9/18 4:51	47 47	11/9/18 5:51 53 11/9/18 5:56 54	12/9/18 6:56 57 12/9/18 23:01 45	14/9/18 0:01 46 14/9/18 0:06 47
8/9/18 2:46	56	9/9/18 3:51	53	10/9/18 4:56	48	11/9/18 6:01 54	12/9/18 23:06 45	14/9/18 0:11 58
8/9/18 2:51	56	9/9/18 3:56	53	10/9/18 5:01	49	11/9/18 6:06 54	12/9/18 23:11 45	14/9/18 0:16 58
8/9/18 2:56 8/9/18 3:01	55 55	9/9/18 4:01 9/9/18 4:06	54 52	10/9/18 5:06 10/9/18 5:11	47 47	11/9/18 6:11 55 11/9/18 6:16 55	12/9/18 23:16 51 12/9/18 23:21 46	14/9/18 0:21 58 14/9/18 0:26 58
	55	9/9/18 4:11	49	10/9/18 5:16	47	11/9/18 6:21 55	12/9/18 23:26 42	14/9/18 0:31 57
8/9/18 3:06 8/9/18 3:11	55	9/9/18 4:16	50	10/9/18 5:21	49	11/9/18 6:26 56	12/9/18 23:31 42	14/9/18 0:36 58

14/9/18 0:41 14/9/18 0:46	<u>e Data</u> 57 57	RTN2a (Hong Kong Electric Cer 15/9/18 1:46 57 15/9/18 1:51 58	16/9/18 2:51 55 16/9/18 2:56 58	17/9/18 3:56 57 17/9/18 4:01 56	18/9/18 5:01 57 18/9/18 5:06 56	19/9/18 6:06 58 19/9/18 6:11 58
14/9/18 0:51	57	15/9/18 1:56 57	16/9/18 3:01 52	17/9/18 4:06 56	18/9/18 5:11 57	19/9/18 6:16 57
14/9/18 0:56 14/9/18 1:01	57 57	15/9/18 2:01 57 15/9/18 2:06 57	16/9/18 3:06 58 16/9/18 3:11 59	17/9/18 4:11 56 17/9/18 4:16 56	18/9/18 5:16 56 18/9/18 5:21 56	19/9/18 6:21 58 19/9/18 6:26 48
14/9/18 1:06	57	15/9/18 2:11 57	16/9/18 3:16 59	17/9/18 4:21 55	18/9/18 5:26 56	19/9/18 6:31 53
14/9/18 1:11	57	15/9/18 2:16 57	16/9/18 3:21 49	17/9/18 4:26 56	18/9/18 5:31 56	19/9/18 6:36 49
14/9/18 1:16	57 57	15/9/18 2:21 58 15/9/18 2:26 57	16/9/18 3:26 55 16/9/18 3:31 57	17/9/18 4:31 58 17/9/18 4:36 57	18/9/18 5:36 57 18/9/18 5:41 56	19/9/18 6:41 45
14/9/18 1:21 14/9/18 1:26	57 57	15/9/18 2:31 57	16/9/18 3:31 57 16/9/18 3:36 52	17/9/18 4:36 57	18/9/18 5:41 56 18/9/18 5:46 56	19/9/18 6:46 58 19/9/18 6:51 53
14/9/18 1:31	57	15/9/18 2:36 57	16/9/18 3:41 54	17/9/18 4:46 55	18/9/18 5:51 56	19/9/18 6:56 52
14/9/18 1:36	57	15/9/18 2:41 57	16/9/18 3:46 58	17/9/18 4:51 56	18/9/18 5:56 40	19/9/18 23:01 49
14/9/18 1:41 14/9/18 1:46	57 57	15/9/18 2:46 57 15/9/18 2:51 57	16/9/18 3:51 55 16/9/18 3:56 51	17/9/18 4:56 56 17/9/18 5:01 43	18/9/18 6:01 56 18/9/18 6:06 57	19/9/18 23:06 51 19/9/18 23:11 52
14/9/18 1:51	57	15/9/18 2:56 57	16/9/18 4:01 60	17/9/18 5:06 56	18/9/18 6:11 56	19/9/18 23:16 51
14/9/18 1:56	57	15/9/18 3:01 57	16/9/18 4:06 59	17/9/18 5:11 55	18/9/18 6:16 57	19/9/18 23:21 57
14/9/18 2:01 14/9/18 2:06	57 57	15/9/18 3:06 57 15/9/18 3:11 57	16/9/18 4:11 54 16/9/18 4:16 57	17/9/18 5:16 55 17/9/18 5:21 56	18/9/18 6:21 58 18/9/18 6:26 58	19/9/18 23:26 51 19/9/18 23:31 54
14/9/18 2:11	57	15/9/18 3:16 57	16/9/18 4:21 60	17/9/18 5:26 56	18/9/18 6:31 47	19/9/18 23:36 44
14/9/18 2:16	58	15/9/18 3:21 57	16/9/18 4:26 58	17/9/18 5:31 56	18/9/18 6:36 58	19/9/18 23:41 44
14/9/18 2:21 14/9/18 2:26	56 56	15/9/18 3:26 58 15/9/18 3:31 57	16/9/18 4:31 54 16/9/18 4:36 52	17/9/18 5:36 57 17/9/18 5:41 55	18/9/18 6:41 58 18/9/18 6:46 58	19/9/18 23:46 46 19/9/18 23:51 51
14/9/18 2:31	57	15/9/18 3:36 57	16/9/18 4:41 57	17/9/18 5:46 57	18/9/18 6:51 58	19/9/18 23:56 46
14/9/18 2:36	57	15/9/18 3:41 57	16/9/18 4:46 57	17/9/18 5:51 56	18/9/18 6:56 52	20/9/18 0:01 58
14/9/18 2:41 14/9/18 2:46	56 57	15/9/18 3:46 57 15/9/18 3:51 58	16/9/18 4:51 57 16/9/18 4:56 54	17/9/18 5:56 56 17/9/18 6:01 42	18/9/18 23:01 51 18/9/18 23:06 48	20/9/18 0:06 41 20/9/18 0:11 43
14/9/18 2:51	57	15/9/18 3:56 57	16/9/18 5:01 57	17/9/18 6:06 57	18/9/18 23:11 46	20/9/18 0:16 58
14/9/18 2:56	56	15/9/18 4:01 57	16/9/18 5:06 51	17/9/18 6:11 57	18/9/18 23:16 45	20/9/18 0:21 58
14/9/18 3:01 14/9/18 3:06	56 56	15/9/18 4:06 57 15/9/18 4:11 57	16/9/18 5:11 48 16/9/18 5:16 53	17/9/18 6:16 57 17/9/18 6:21 56	18/9/18 23:21 50 18/9/18 23:26 55	20/9/18 0:26 58 20/9/18 0:31 58
14/9/18 3:11	57	15/9/18 4:16 47	16/9/18 5:21 58	17/9/18 6:26 56	18/9/18 23:31 49	20/9/18 0:36 58
14/9/18 3:16	57	15/9/18 4:21 58	16/9/18 5:26 58	17/9/18 6:31 56	18/9/18 23:36 50	20/9/18 0:41 58
14/9/18 3:21	56 57	15/9/18 4:26 57 15/9/18 4:31 57	16/9/18 5:31 52 16/9/18 5:36 51	17/9/18 6:36 56 17/9/18 6:41 57	18/9/18 23:41 55 18/9/18 23:46 53	20/9/18 0:46 58 20/9/18 0:51 58
14/9/18 3:26 14/9/18 3:31	57 56	15/9/18 4:36 57	16/9/18 5:36 51	17/9/18 6:41 57	18/9/18 23:46 53	20/9/18 0:51 58
14/9/18 3:36	56	15/9/18 4:41 57	16/9/18 5:46 57	17/9/18 6:51 57	18/9/18 23:56 58	20/9/18 1:01 57
14/9/18 3:41	56	15/9/18 4:46 57	16/9/18 5:51 55 16/9/18 5:56 55	17/9/18 6:56 57 17/9/18 23:01 45	19/9/18 0:01 58	20/9/18 1:06 57
14/9/18 3:46 14/9/18 3:51	56 56	15/9/18 4:51 57 15/9/18 4:56 57	16/9/18 5:56 55 16/9/18 6:01 60	17/9/18 23:01 45 17/9/18 23:06 58	19/9/18 0:06 58 19/9/18 0:11 57	20/9/18 1:11 57 20/9/18 1:16 57
14/9/18 3:56	56	15/9/18 5:01 57	16/9/18 6:06 57	17/9/18 23:11 58	19/9/18 0:16 58	20/9/18 1:21 57
14/9/18 4:01	56	15/9/18 5:06 57	16/9/18 6:11 52	17/9/18 23:16 58 17/9/18 23:21 57	19/9/18 0:21 50 19/9/18 0:26 58	20/9/18 1:26 57 20/9/18 1:31 57
14/9/18 4:06 14/9/18 4:11	56 56	15/9/18 5:11 57 15/9/18 5:16 57	16/9/18 6:16 58 16/9/18 6:21 61	17/9/18 23:26 58	19/9/18 0:26 58 19/9/18 0:31 58	20/9/18 1:31 57 20/9/18 1:36 57
14/9/18 4:16	56	15/9/18 5:21 57	16/9/18 6:26 59	17/9/18 23:31 54	19/9/18 0:36 58	20/9/18 1:41 57
14/9/18 4:21	56 57	15/9/18 5:26 57 15/9/18 5:31 57	16/9/18 6:31 57 16/9/18 6:36 62	17/9/18 23:36 58 17/9/18 23:41 58	19/9/18 0:41 49	20/9/18 1:46 57 20/9/18 1:51 57
14/9/18 4:26 14/9/18 4:31	57 56	15/9/18 5:31 57 15/9/18 5:36 57	16/9/18 6:36 62 16/9/18 6:41 60	17/9/18 23:41 58	19/9/18 0:46 58 19/9/18 0:51 58	20/9/18 1:51 57 20/9/18 1:56 57
14/9/18 4:36	56	15/9/18 5:41 57	16/9/18 6:46 66	17/9/18 23:51 51	19/9/18 0:56 57	20/9/18 2:01 57
14/9/18 4:41	56	15/9/18 5:46 57	16/9/18 6:51 60	17/9/18 23:56 52	19/9/18 1:01 58	20/9/18 2:06 57
14/9/18 4:46 14/9/18 4:51	56 56	15/9/18 5:51 57 15/9/18 5:56 57	16/9/18 6:56 65 16/9/18 23:01 57	18/9/18 0:01 58 18/9/18 0:06 57	19/9/18 1:06 47 19/9/18 1:11 58	20/9/18 2:11 57 20/9/18 2:16 57
14/9/18 4:56	56	15/9/18 6:01 58	16/9/18 23:06 58	18/9/18 0:11 57	19/9/18 1:16 51	20/9/18 2:21 57
14/9/18 5:01	56 56	15/9/18 6:06 57 15/9/18 6:11 58	16/9/18 23:11 39 16/9/18 23:16 57	18/9/18 0:16 58 18/9/18 0:21 58	19/9/18 1:21 58 19/9/18 1:26 58	20/9/18 2:26 57 20/9/18 2:31 57
14/9/18 5:06 14/9/18 5:11	56	15/9/18 6:11 58 15/9/18 6:16 58	16/9/18 23:21 56	18/9/18 0:21 58 18/9/18 0:26 53	19/9/18 1:26 58 19/9/18 1:31 52	20/9/18 2:31 57 20/9/18 2:36 56
14/9/18 5:16	56	15/9/18 6:21 57	16/9/18 23:26 56	18/9/18 0:31 58	19/9/18 1:36 57	20/9/18 2:41 57
14/9/18 5:21 14/9/18 5:26	56 57	15/9/18 6:26 58 15/9/18 6:31 53	16/9/18 23:31 56 16/9/18 23:36 56	18/9/18 0:36 57 18/9/18 0:41 57	19/9/18 1:41 57 19/9/18 1:46 58	20/9/18 2:46 57 20/9/18 2:51 57
14/9/18 5:31	56	15/9/18 6:36 58	16/9/18 23:41 56	18/9/18 0:46 57	19/9/18 1:51 58	20/9/18 2:56 57
14/9/18 5:36	56	15/9/18 6:41 53	16/9/18 23:46 57	18/9/18 0:51 57	19/9/18 1:56 58	20/9/18 3:01 57
14/9/18 5:41 14/9/18 5:46	56 56	15/9/18 6:46 43 15/9/18 6:51 51	16/9/18 23:51 57 16/9/18 23:56 57	18/9/18 0:56 57 18/9/18 1:01 57	19/9/18 2:01 57 19/9/18 2:06 57	20/9/18 3:06 57 20/9/18 3:11 57
14/9/18 5:51	56	15/9/18 6:56 58	17/9/18 0:01 58	18/9/18 1:06 57	19/9/18 2:11 57	20/9/18 3:16 56
14/9/18 5:56	57	15/9/18 23:01 54	17/9/18 0:06 56	18/9/18 1:11 57	19/9/18 2:16 57	20/9/18 3:21 56
14/9/18 6:01 14/9/18 6:06	56 57	15/9/18 23:06 47 15/9/18 23:11 52	17/9/18 0:11 56 17/9/18 0:16 56	18/9/18 1:16 57 18/9/18 1:21 57	19/9/18 2:21 57 19/9/18 2:26 56	20/9/18 3:26 56 20/9/18 3:31 56
14/9/18 6:11	58	15/9/18 23:16 48	17/9/18 0:21 49	18/9/18 1:26 58	19/9/18 2:31 57	20/9/18 3:36 56
14/9/18 6:16	57	15/9/18 23:21 52	17/9/18 0:26 58	18/9/18 1:31 57	19/9/18 2:36 57	20/9/18 3:41 56
14/9/18 6:21 14/9/18 6:26	58 57	15/9/18 23:26 51 15/9/18 23:31 52	17/9/18 0:31 50 17/9/18 0:36 57	18/9/18 1:36 57 18/9/18 1:41 58	19/9/18 2:41 57 19/9/18 2:46 57	20/9/18 3:46 56 20/9/18 3:51 56
14/9/18 6:31	57	15/9/18 23:36 46	17/9/18 0:41 57	18/9/18 1:46 57	19/9/18 2:51 57	20/9/18 3:56 56
14/9/18 6:36	58	15/9/18 23:41 51	17/9/18 0:46 56	18/9/18 1:51 57	19/9/18 2:56 57	20/9/18 4:01 56
14/9/18 6:41 14/9/18 6:46	58 48	15/9/18 23:46 50 15/9/18 23:51 50	17/9/18 0:51 58 17/9/18 0:56 56	18/9/18 1:56 57 18/9/18 2:01 56	19/9/18 3:01 57 19/9/18 3:06 56	20/9/18 4:06 44 20/9/18 4:11 57
14/9/18 6:51	53	15/9/18 23:56 53	17/9/18 1:01 62	18/9/18 2:06 56	19/9/18 3:11 57	20/9/18 4:16 58
14/9/18 6:56	37	16/9/18 0:01 49	17/9/18 1:06 61	18/9/18 2:11 56	19/9/18 3:16 57	20/9/18 4:21 57
14/9/18 23:01 14/9/18 23:06	54 53	16/9/18 0:06 42 16/9/18 0:11 43	17/9/18 1:11 58 17/9/18 1:16 56	18/9/18 2:16 57 18/9/18 2:21 55	19/9/18 3:21 56 19/9/18 3:26 57	20/9/18 4:26 57 20/9/18 4:31 57
14/9/18 23:11	50	16/9/18 0:16 53	17/9/18 1:21 57	18/9/18 2:26 57	19/9/18 3:31 56	20/9/18 4:36 49
14/9/18 23:16	57	16/9/18 0:21 55	17/9/18 1:26 56	18/9/18 2:31 57	19/9/18 3:36 56	20/9/18 4:41 57
14/9/18 23:21 14/9/18 23:26	54 51	16/9/18 0:26 57 16/9/18 0:31 57	17/9/18 1:31 56 17/9/18 1:36 56	18/9/18 2:36 56 18/9/18 2:41 57	19/9/18 3:41 56 19/9/18 3:46 56	20/9/18 4:46 57 20/9/18 4:51 57
14/9/18 23:31	50	16/9/18 0:36 55	17/9/18 1:41 56	18/9/18 2:46 57	19/9/18 3:51 56	20/9/18 4:56 56
14/9/18 23:36	45	16/9/18 0:41 58	17/9/18 1:46 56	18/9/18 2:51 56	19/9/18 3:56 56	20/9/18 5:01 56
14/9/18 23:41 14/9/18 23:46	58 47	16/9/18 0:46 58 16/9/18 0:51 58	17/9/18 1:51 56 17/9/18 1:56 58	18/9/18 2:56 57 18/9/18 3:01 56	19/9/18 4:01 56 19/9/18 4:06 56	20/9/18 5:06 57 20/9/18 5:11 57
14/9/18 23:51	58	16/9/18 0:56 58	17/9/18 2:01 58	18/9/18 3:06 56	19/9/18 4:11 57	20/9/18 5:16 56
14/9/18 23:56 15/9/18 0:01	58	16/9/18 1:01 48 16/9/18 1:06 50	17/9/18 2:06 56 17/9/18 2:11 56	18/9/18 3:11 56 18/9/18 3:16 57	19/9/18 4:16 57 19/9/18 4:21 56	20/9/18 5:21 57 20/9/18 5:26 57
15/9/18 0:06	44 52	16/9/18 1:06 50 16/9/18 1:11 52	17/9/18 2:11 56	18/9/18 3:16 57 18/9/18 3:21 56	19/9/18 4:21 56 19/9/18 4:26 56	20/9/18 5:26 57 20/9/18 5:31 56
15/9/18 0:11	44	16/9/18 1:16 37	17/9/18 2:21 55	18/9/18 3:26 58	19/9/18 4:31 56	20/9/18 5:36 56
15/9/18 0:16 15/9/18 0:21	39 58	16/9/18 1:21 51 16/9/18 1:26 48	17/9/18 2:26 57 17/9/18 2:31 55	18/9/18 3:31 49 18/9/18 3:36 56	19/9/18 4:36 57 19/9/18 4:41 56	20/9/18 5:41 57 20/9/18 5:46 57
15/9/18 0:21	58 43	16/9/18 1:31 50	17/9/18 2:31 55	18/9/18 3:36 56	19/9/18 4:41 56	20/9/18 5:46 57 20/9/18 5:51 39
15/9/18 0:31	46	16/9/18 1:36 54	17/9/18 2:41 56	18/9/18 3:46 57	19/9/18 4:51 56	20/9/18 5:56 55
15/9/18 0:36 15/9/18 0:41	58 58	16/9/18 1:41 48 16/9/18 1:46 53	17/9/18 2:46 55 17/9/18 2:51 55	18/9/18 3:51 56 18/9/18 3:56 56	19/9/18 4:56 57 19/9/18 5:01 57	20/9/18 6:01 58 20/9/18 6:06 58
15/9/18 0:46	58	16/9/18 1:51 58	17/9/18 2:56 55	18/9/18 4:01 58	19/9/18 5:06 56	20/9/18 6:11 58
15/9/18 0:51	50	16/9/18 1:56 57	17/9/18 3:01 56	18/9/18 4:06 56	19/9/18 5:11 56	20/9/18 6:16 54
15/9/18 0:56	58 58	16/9/18 2:01 47 16/9/18 2:06 52	17/9/18 3:06 56 17/9/18 3:11 57	18/9/18 4:11 57 18/9/18 4:16 57	19/9/18 5:16 56 19/9/18 5:21 57	20/9/18 6:21 58 20/9/18 6:26 58
15/9/18 1:01 15/9/18 1:06	58 58	16/9/18 2:06 52 16/9/18 2:11 52	17/9/18 3:11 57 17/9/18 3:16 56	18/9/18 4:16 57 18/9/18 4:21 56	19/9/18 5:21 57 19/9/18 5:26 57	20/9/18 6:26 58 20/9/18 6:31 58
15/9/18 1:11	58	16/9/18 2:16 53	17/9/18 3:21 58	18/9/18 4:26 57	19/9/18 5:31 56	20/9/18 6:36 58
15/9/18 1:16	57 48	16/9/18 2:21 53 16/9/18 2:26 48	17/9/18 3:26 52	18/9/18 4:31 58 18/9/18 4:36 55	19/9/18 5:36 57 19/9/18 5:41 57	20/9/18 6:41 58
15/9/18 1:21 15/9/18 1:26	48 47	16/9/18 2:26 48 16/9/18 2:31 58	17/9/18 3:31 56 17/9/18 3:36 58	18/9/18 4:36 55 18/9/18 4:41 56	19/9/18 5:41 57 19/9/18 5:46 57	20/9/18 6:46 32 20/9/18 6:51 41
	58	16/9/18 2:36 56	17/9/18 3:41 49	18/9/18 4:46 56	19/9/18 5:51 57	20/9/18 6:56 39
15/9/18 1:31				10/0/10/061 57	10/0/10 5-50 50	20/9/18 23:01 57
15/9/18 1:31 15/9/18 1:36 15/9/18 1:41	58 58	16/9/18 2:41 58 16/9/18 2:46 53	17/9/18 3:46 61 17/9/18 3:51 59	18/9/18 4:51 57 18/9/18 4:56 56	19/9/18 5:56 56 19/9/18 6:01 53	20/9/18 23:06 52

Real-time Noise Data 20/9/18 23:11 51	RTN2a (Hong Kong Electric Cen 22/9/18 0:16 49	tre) 23/9/18 1:21 58	24/9/18 2:26 52	25/9/18 3:31 55	26/9/18 4:36 55
20/9/18 23:16 56	22/9/18 0:21 58	23/9/18 1:26 58	24/9/18 2:31 57	25/9/18 3:36 54	26/9/18 4:41 54
20/9/18 23:21 52 20/9/18 23:26 53	22/9/18 0:26 47 22/9/18 0:31 53	23/9/18 1:31 58 23/9/18 1:36 58	24/9/18 2:36 56 24/9/18 2:41 56	25/9/18 3:41 55 25/9/18 3:46 53	26/9/18 4:46 53 26/9/18 4:51 55
20/9/18 23:31 50	22/9/18 0:36 56	23/9/18 1:41 55	24/9/18 2:46 56	25/9/18 3:51 52	26/9/18 4:56 55
20/9/18 23:36 49 20/9/18 23:41 48	22/9/18 0:41 56 22/9/18 0:46 58	23/9/18 1:46 58 23/9/18 1:51 50	24/9/18 2:51 57 24/9/18 2:56 57	25/9/18 3:56 54 25/9/18 4:01 54	26/9/18 5:01 55 26/9/18 5:06 53
20/9/18 23:46 40	22/9/18 0:51 47	23/9/18 1:56 57	24/9/18 3:01 56	25/9/18 4:06 55	26/9/18 5:11 53
20/9/18 23:51 52 20/9/18 23:56 54	22/9/18 0:56 58 22/9/18 1:01 58	23/9/18 2:01 57 23/9/18 2:06 53	24/9/18 3:06 56 24/9/18 3:11 56	25/9/18 4:11 55 25/0/18 4:16 55	26/9/18 5:16 52 26/9/18 5:21 55
21/9/18 0:01 50	22/9/18 1:06 58	23/9/18 2:06 55	24/9/18 3:16 57	25/9/18 4:16 55 25/9/18 4:21 56	26/9/18 5:21 55 26/9/18 5:26 54
21/9/18 0:06 45	22/9/18 1:11 39	23/9/18 2:16 57	24/9/18 3:21 57	25/9/18 4:26 57	26/9/18 5:31 53
21/9/18 0:11 58 21/9/18 0:16 58	22/9/18 1:16 58 22/9/18 1:21 58	23/9/18 2:21 57 23/9/18 2:26 58	24/9/18 3:26 57 24/9/18 3:31 57	25/9/18 4:31 56 25/9/18 4:36 55	26/9/18 5:36 52 26/9/18 5:41 54
21/9/18 0:21 58	22/9/18 1:26 58	23/9/18 2:31 57	24/9/18 3:36 56	25/9/18 4:41 55	26/9/18 5:46 53
21/9/18 0:26 42 21/9/18 0:31 58	22/9/18 1:31 58 22/9/18 1:36 58	23/9/18 2:36 57 23/9/18 2:41 57	24/9/18 3:41 56 24/9/18 3:46 56	25/9/18 4:46 55 25/9/18 4:51 56	26/9/18 5:51 54 26/9/18 5:56 54
21/9/18 0:36 58	22/9/18 1:41 58	23/9/18 2:46 57	24/9/18 3:51 56	25/9/18 4:56 55	26/9/18 6:01 54
21/9/18 0:41 58 21/9/18 0:46 51	22/9/18 1:46 58 22/9/18 1:51 58	23/9/18 2:51 57 23/9/18 2:56 58	24/9/18 3:56 56 24/9/18 4:01 56	25/9/18 5:01 54 25/9/18 5:06 56	26/9/18 6:06 57 26/9/18 6:11 57
21/9/18 0:51 48	22/9/18 1:56 58	23/9/18 2:30 57	24/9/18 4:06 56	25/9/18 5:11 56	26/9/18 6:16 56
21/9/18 0:56 58	22/9/18 2:01 58	23/9/18 3:06 57	24/9/18 4:11 56	25/9/18 5:16 55	26/9/18 6:21 54
21/9/18 1:01 58 21/9/18 1:06 58	22/9/18 2:06 46 22/9/18 2:11 52	23/9/18 3:11 57 23/9/18 3:16 57	24/9/18 4:16 56 24/9/18 4:21 56	25/9/18 5:21 53 25/9/18 5:26 53	26/9/18 6:26 55 26/9/18 6:31 55
21/9/18 1:11 58	22/9/18 2:16 58	23/9/18 3:21 57	24/9/18 4:26 56	25/9/18 5:31 54	26/9/18 6:36 57
21/9/18 1:16 57 21/9/18 1:21 58	22/9/18 2:21 58 22/9/18 2:26 57	23/9/18 3:26 57 23/9/18 3:31 57	24/9/18 4:31 56 24/9/18 4:36 56	25/9/18 5:36 55 25/9/18 5:41 57	26/9/18 6:41 57 26/9/18 6:46 57
21/9/18 1:26 58	22/9/18 2:31 57	23/9/18 3:36 57	24/9/18 4:41 56	25/9/18 5:46 56	26/9/18 6:51 57
21/9/18 1:31 57 21/9/18 1:36 58	22/9/18 2:36 57 22/9/18 2:41 57	23/9/18 3:41 57 23/9/18 3:46 57	24/9/18 4:46 56 24/9/18 4:51 56	25/9/18 5:51 56 25/9/18 5:56 55	26/9/18 6:56 59 26/9/18 23:01 59
21/9/18 1:41 57	22/9/18 2:46 57	23/9/18 3:51 57	24/9/18 4:56 57	25/9/18 6:01 56	26/9/18 23:06 58
21/9/18 1:46 57	22/9/18 2:51 57	23/9/18 3:56 57	24/9/18 5:01 57	25/9/18 6:06 56 25/9/18 6:11 56	26/9/18 23:11 61
21/9/18 1:51 57 21/9/18 1:56 57	22/9/18 2:56 57 22/9/18 3:01 57	23/9/18 4:01 57 23/9/18 4:06 57	24/9/18 5:06 57 24/9/18 5:11 57	25/9/18 6:11 56 25/9/18 6:16 56	26/9/18 23:16 58 26/9/18 23:21 58
21/9/18 2:01 57	22/9/18 3:06 57	23/9/18 4:11 56	24/9/18 5:16 57	25/9/18 6:21 56	26/9/18 23:26 57
21/9/18 2:06 57 21/9/18 2:11 57	22/9/18 3:11 57 22/9/18 3:16 57	23/9/18 4:16 56 23/9/18 4:21 57	24/9/18 5:21 57 24/9/18 5:26 57	25/9/18 6:26 55 25/9/18 6:31 57	26/9/18 23:31 57 26/9/18 23:36 57
21/9/18 2:16 57	22/9/18 3:10 57	23/9/18 4:26 57	24/9/18 5:31 57	25/9/18 6:36 57	26/9/18 23:41 57
21/9/18 2:21 57	22/9/18 3:26 57	23/9/18 4:31 57	24/9/18 5:36 57	25/9/18 6:41 55	26/9/18 23:46 57
21/9/18 2:26 57 21/9/18 2:31 57	22/9/18 3:31 57 22/9/18 3:36 57	23/9/18 4:36 57 23/9/18 4:41 57	24/9/18 5:41 57 24/9/18 5:46 57	25/9/18 6:46 57 25/9/18 6:51 56	26/9/18 23:51 57 26/9/18 23:56 56
21/9/18 2:36 57	22/9/18 3:41 57	23/9/18 4:46 57	24/9/18 5:51 57	25/9/18 6:56 57	20,0,10 20,000 00
21/9/18 2:41 57 21/9/18 2:46 56	22/9/18 3:46 57 22/9/18 3:51 58	23/9/18 4:51 57 23/9/18 4:56 57	24/9/18 5:56 57 24/9/18 6:01 57	25/9/18 23:01 58 25/9/18 23:06 59	
21/9/18 2:51 57	22/9/18 3:56 57	23/9/18 5:01 57	24/9/18 6:06 58	25/9/18 23:06 59	
21/9/18 2:56 57	22/9/18 4:01 57	23/9/18 5:06 57	24/9/18 6:11 58	25/9/18 23:16 56	
21/9/18 3:01 57 21/9/18 3:06 57	22/9/18 4:06 57 22/9/18 4:11 56	23/9/18 5:11 57 23/9/18 5:16 57	24/9/18 6:16 52 24/9/18 6:21 57	25/9/18 23:21 57 25/9/18 23:26 57	
21/9/18 3:11 57	22/9/18 4:16 56	23/9/18 5:21 56	24/9/18 6:26 58	25/9/18 23:31 57	
21/9/18 3:16 57 21/9/18 3:21 57	22/9/18 4:21 57 22/9/18 4:26 57	23/9/18 5:26 56 23/9/18 5:31 57	24/9/18 6:31 58 24/9/18 6:36 58	25/9/18 23:36 57 25/9/18 23:41 56	
21/9/18 3:26 57	22/9/18 4:20 57	23/9/18 5:36 56	24/9/18 6:41 45	25/9/18 23:41 56	
21/9/18 3:31 57	22/9/18 4:36 57	23/9/18 5:41 57	24/9/18 6:46 51	25/9/18 23:51 57	
21/9/18 3:36 56 21/9/18 3:41 56	22/9/18 4:41 57 22/9/18 4:46 57	23/9/18 5:46 57 23/9/18 5:51 57	24/9/18 6:51 49 24/9/18 6:56 48	25/9/18 23:56 57 26/9/18 0:01 57	
21/9/18 3:46 57	22/9/18 4:51 56	23/9/18 5:56 57	24/9/18 23:01 60	26/9/18 0:06 56	
21/9/18 3:51 57	22/9/18 4:56 56	23/9/18 6:01 57 23/9/18 6:06 56	24/9/18 23:06 60	26/9/18 0:11 58 26/0/18 0:16 57	
21/9/18 3:56 57 21/9/18 4:01 56	22/9/18 5:01 56 22/9/18 5:06 56	23/9/18 6:06 56 23/9/18 6:11 57	24/9/18 23:11 58 24/9/18 23:16 57	26/9/18 0:16 57 26/9/18 0:21 57	
21/9/18 4:06 56	22/9/18 5:11 57	23/9/18 6:16 57	24/9/18 23:21 57	26/9/18 0:26 55	
21/9/18 4:11 56 21/9/18 4:16 56	22/9/18 5:16 57 22/9/18 5:21 54	23/9/18 6:21 43 23/9/18 6:26 57	24/9/18 23:26 58 24/9/18 23:31 60	26/9/18 0:31 57 26/9/18 0:36 57	
21/9/18 4:21 56	22/9/18 5:26 58	23/9/18 6:31 58	24/9/18 23:36 61	26/9/18 0:41 56	
21/9/18 4:26 57 21/9/18 4:31 57	22/9/18 5:31 57 22/9/18 5:36 57	23/9/18 6:36 58 23/9/18 6:41 58	24/9/18 23:41 59 24/9/18 23:46 58	26/9/18 0:46 58 26/9/18 0:51 55	
21/9/18 4:31 57 21/9/18 4:36 56	22/9/18 5:36 57 22/9/18 5:41 58	23/9/18 6:41 58 23/9/18 6:46 58	24/9/18 23:46 58 24/9/18 23:51 59	26/9/18 0:51 55 26/9/18 0:56 54	
21/9/18 4:41 56	22/9/18 5:46 57	23/9/18 6:51 58	24/9/18 23:56 58	26/9/18 1:01 56	
21/9/18 4:46 57 21/9/18 4:51 57	22/9/18 5:51 58 22/9/18 5:56 57	23/9/18 6:56 48 23/9/18 23:01 57	25/9/18 0:01 57 25/9/18 0:06 57	26/9/18 1:06 57 26/9/18 1:11 56	
21/9/18 4:56 57	22/9/18 6:01 57	23/9/18 23:06 46	25/9/18 0:11 58	26/9/18 1:16 55	
21/9/18 5:01 56 21/9/18 5:06 57	22/9/18 6:06 58 22/9/18 6:11 58	23/9/18 23:11 56 23/9/18 23:16 32	25/9/18 0:16 58 25/9/18 0:21 59	26/9/18 1:21 55 26/9/18 1:26 55	
21/9/18 5:06 57 21/9/18 5:11 56	22/9/18 6:11 58 22/9/18 6:16 57	23/9/18 23:16 32 23/9/18 23:21 47	25/9/18 0:21 59 25/9/18 0:26 58	26/9/18 1:26 55 26/9/18 1:31 55	
21/9/18 5:16 56	22/9/18 6:21 58	23/9/18 23:26 58	25/9/18 0:31 59	26/9/18 1:36 55	
21/9/18 5:21 56 21/9/18 5:26 57	22/9/18 6:26 58 22/9/18 6:31 57	23/9/18 23:31 39 23/9/18 23:36 58	25/9/18 0:36 57 25/9/18 0:41 71	26/9/18 1:41 54 26/9/18 1:46 56	
21/9/18 5:31 57	22/9/18 6:36 58	23/9/18 23:41 58	25/9/18 0:46 71	26/9/18 1:51 57	
21/9/18 5:36 35 21/9/18 5:41 58	22/9/18 6:41 50 22/9/18 6:46 55	23/9/18 23:46 42 23/9/18 23:51 58	25/9/18 0:51 62 25/9/18 0:56 58	26/9/18 1:56 55 26/9/18 2:01 52	
21/9/18 5:46 58	22/9/18 6:51 51	23/9/18 23:56 58	25/9/18 1:01 58	26/9/18 2:06 55	
21/9/18 5:51 58	22/9/18 6:56 54	24/9/18 0:01 58	25/9/18 1:06 56	26/9/18 2:11 55	
21/9/18 5:56 57 21/9/18 6:01 57	22/9/18 23:01 51 22/9/18 23:06 49	24/9/18 0:06 42 24/9/18 0:11 58	25/9/18 1:11 55 25/9/18 1:16 59	26/9/18 2:16 54 26/9/18 2:21 55	
21/9/18 6:06 58	22/9/18 23:11 49	24/9/18 0:16 58	25/9/18 1:21 57	26/9/18 2:26 56	
21/9/18 6:11 58 21/9/18 6:16 48	22/9/18 23:16 57 22/9/18 23:21 56	24/9/18 0:21 58 24/9/18 0:26 58	25/9/18 1:26 57 25/9/18 1:31 57	26/9/18 2:31 54 26/9/18 2:36 55	
21/9/18 6:21 45	22/9/18 23:26 54	24/9/18 0:31 48	25/9/18 1:36 60	26/9/18 2:41 54	
21/9/18 6:26 45	22/9/18 23:31 50	24/9/18 0:36 58	25/9/18 1:41 58	26/9/18 2:46 53	
21/9/18 6:31 58 21/9/18 6:36 44	22/9/18 23:36 54 22/9/18 23:41 52	24/9/18 0:41 57 24/9/18 0:46 57	25/9/18 1:46 56 25/9/18 1:51 56	26/9/18 2:51 53 26/9/18 2:56 54	
21/9/18 6:41 49	22/9/18 23:46 52	24/9/18 0:51 58	25/9/18 1:56 57	26/9/18 3:01 55	
21/9/18 6:46 32 21/9/18 6:51 45	22/9/18 23:51 55 22/9/18 23:56 59	24/9/18 0:56 58 24/9/18 1:01 58	25/9/18 2:01 58 25/9/18 2:06 59	26/9/18 3:06 53 26/9/18 3:11 54	
21/9/18 6:56 58	23/9/18 0:01 44	24/9/18 1:06 58	25/9/18 2:11 64	26/9/18 3:16 56	
21/9/18 23:01 54	23/9/18 0:06 49 23/9/18 0:11 47	24/9/18 1:11 58 24/9/18 1:16 58	25/9/18 2:16 59 25/9/18 2:21 56	26/9/18 3:21 56 26/9/18 3:26 55	
21/9/18 23:06 55 21/9/18 23:11 58	23/9/18 0:11 47 23/9/18 0:16 48	24/9/18 1:16 58 24/9/18 1:21 57	25/9/18 2:21 56 25/9/18 2:26 62	26/9/18 3:26 55 26/9/18 3:31 54	
21/9/18 23:16 59	23/9/18 0:21 58	24/9/18 1:26 58	25/9/18 2:31 65	26/9/18 3:36 52	
21/9/18 23:21 56 21/9/18 23:26 55	23/9/18 0:26 40 23/9/18 0:31 46	24/9/18 1:31 58 24/9/18 1:36 57	25/9/18 2:36 63 25/9/18 2:41 60	26/9/18 3:41 55 26/9/18 3:46 55	
21/9/18 23:31 54	23/9/18 0:36 51	24/9/18 1:41 57	25/9/18 2:46 57	26/9/18 3:51 54	
21/9/18 23:36 56	23/9/18 0:41 43	24/9/18 1:46 57	25/9/18 2:51 56	26/9/18 3:56 53	
21/9/18 23:41 54 21/9/18 23:46 54	23/9/18 0:46 58 23/9/18 0:51 58	24/9/18 1:51 57 24/9/18 1:56 56	25/9/18 2:56 56 25/9/18 3:01 56	26/9/18 4:01 54 26/9/18 4:06 52	
21/9/18 23:51 44	23/9/18 0:56 35	24/9/18 2:01 56	25/9/18 3:06 59	26/9/18 4:11 54	
21/9/18 23:56 51 22/9/18 0:01 52	23/9/18 1:01 58 23/9/18 1:06 45	24/9/18 2:06 56 24/9/18 2:11 57	25/9/18 3:11 56 25/9/18 3:16 55	26/9/18 4:16 53 26/9/18 4:21 54	
22/9/18 0:06 50	23/9/18 1:11 46	24/9/18 2:16 57	25/9/18 3:21 54	26/9/18 4:26 53	
22/9/18 0:11 46	23/9/18 1:16 57	24/9/18 2:21 58	25/9/18 3:26 56	26/9/18 4:31 52	I

Real-time Noise Data	RTN3 (Po Leung Kuk Yu Lee Mo	Fan Memorial School)			
Normal Day 07:00-19:00	31/8/18 12:31 67	6/9/18 7:01 69 6/0/18 7:01 50	11/9/18 13:31 69	17/9/18 8:01 69	21/9/18 14:31 67
27/8/18 7:01 69	31/8/18 13:01 69 31/8/18 13:31 68	6/9/18 7:31 59 6/9/18 8:01 69	11/9/18 14:01 69 11/9/18 14:31 70	17/9/18 8:31 69 17/9/18 9:01 69	21/9/18 15:01 67 21/9/18 15:31 67
27/8/18 7:31 69	31/8/18 14:01 68	6/9/18 8:31 68	11/9/18 15:01 69	17/9/18 9:31 69	21/9/18 16:01 67
27/8/18 8:01 68 27/8/18 8:31 67	31/8/18 14:31 67 31/8/18 15:01 67	6/9/18 9:01 69 6/9/18 9:31 58	11/9/18 15:31 67 11/9/18 16:01 67	17/9/18 10:01 69 17/9/18 10:31 69	21/9/18 16:31 68 21/9/18 17:01 66
27/8/18 9:01 69	31/8/18 15:31 66	6/9/18 10:01 69	11/9/18 16:31 68	17/9/18 11:01 69	21/9/18 17:31 66
27/8/18 9:31 54 27/8/18 10:01 65	31/8/18 16:01 68 31/8/18 16:31 69	6/9/18 10:31 59 6/0/18 11:01 56	11/9/18 17:01 69 11/9/18 17:31 69	17/9/18 11:31 69 17/9/18 12:01 69	21/9/18 18:01 65 21/9/18 18:31 66
27/8/18 10:01 65 27/8/18 10:31 68	31/8/18 16:31 69 31/8/18 17:01 68	6/9/18 11:01 56 6/9/18 11:31 54	11/9/18 17:31 69	17/9/18 12:01 69 17/9/18 12:31 69	21/9/18 18:31 66 22/9/18 7:01 68
27/8/18 11:01 69	31/8/18 17:31 68	6/9/18 12:01 70	11/9/18 18:31 69	17/9/18 13:01 69	22/9/18 7:31 69
27/8/18 11:31 56 27/8/18 12:01 69	31/8/18 18:01 69 31/8/18 18:31 68	6/9/18 12:31 55 6/9/18 13:01 51	12/9/18 7:01 68 12/9/18 7:31 70	17/9/18 13:31 69 17/9/18 14:01 68	22/9/18 8:01 69 22/9/18 8:31 69
27/8/18 12:31 70	1/9/18 7:01 69	6/9/18 13:31 53	12/9/18 8:01 69	17/9/18 14:31 68	22/9/18 9:01 43
27/8/18 13:01 69 27/8/18 13:31 69	1/9/18 7:31 69 1/9/18 8:01 60	6/9/18 14:01 70 6/9/18 14:31 69	12/9/18 8:31 67 12/9/18 9:01 69	17/9/18 15:01 69 17/9/18 15:31 69	22/9/18 9:31 55 22/9/18 10:01 68
27/8/18 14:01 60	1/9/18 8:31 59	6/9/18 15:01 69	12/9/18 9:31 55	17/9/18 16:01 68	22/9/18 10:31 68
27/8/18 14:31 69 27/8/18 15:01 69	1/9/18 9:01 64 1/9/18 9:31 67	6/9/18 15:31 59 6/9/18 16:01 52	12/9/18 10:01 69 12/9/18 10:31 69	17/9/18 16:31 68 17/9/18 17:01 68	22/9/18 11:01 69 22/9/18 11:31 68
27/8/18 15:31 69	1/9/18 9:31 67	6/9/18 16:31 69	12/9/18 11:01 69	17/9/18 17:31 68	22/9/18 12:01 67
27/8/18 16:01 69	1/9/18 10:31 68	6/9/18 17:01 58	12/9/18 11:31 69	17/9/18 18:01 68	22/9/18 12:31 66
27/8/18 16:31 69 27/8/18 17:01 69	1/9/18 11:01 69 1/9/18 11:31 68	6/9/18 17:31 50 6/9/18 18:01 69	12/9/18 12:01 69 12/9/18 12:31 70	17/9/18 18:31 68 18/9/18 7:01 69	22/9/18 13:01 68 22/9/18 13:31 66
27/8/18 17:31 69	1/9/18 12:01 69	6/9/18 18:31 69	12/9/18 13:01 54	18/9/18 7:31 70	22/9/18 14:01 68
27/8/18 18:01 69 27/8/18 18:31 69	1/9/18 12:31 69 1/9/18 13:01 65	7/9/18 7:01 68 7/9/18 7:31 55	12/9/18 13:31 52 12/9/18 14:01 69	18/9/18 8:01 69 18/9/18 8:31 67	22/9/18 14:31 69 22/9/18 15:01 67
28/8/18 7:01 54	1/9/18 13:31 66	7/9/18 8:01 69	12/9/18 14:31 69	18/9/18 9:01 68	22/9/18 15:31 69
28/8/18 7:31 60 28/8/18 8:01 68	1/9/18 14:01 55 1/9/18 14:31 61	7/9/18 8:31 68 7/9/18 9:01 68	12/9/18 15:01 68 12/9/18 15:31 51	18/9/18 9:31 53 18/9/18 10:01 70	22/9/18 16:01 69 22/9/18 16:31 69
28/8/18 8:31 68	1/9/18 15:01 56	7/9/18 9:31 69	12/9/18 16:01 58	18/9/18 10:31 59	22/9/18 17:01 69
28/8/18 9:01 69	1/9/18 15:31 69	7/9/18 10:01 69	12/9/18 16:31 60	18/9/18 11:01 70	22/9/18 17:31 69
28/8/18 9:31 70 28/8/18 10:01 50	1/9/18 16:01 68 1/9/18 16:31 69	7/9/18 10:31 68 7/9/18 11:01 68	12/9/18 17:01 57 12/9/18 17:31 69	18/9/18 11:31 70 18/9/18 12:01 69	22/9/18 18:01 69 22/9/18 18:31 68
28/8/18 10:31 58	1/9/18 17:01 52	7/9/18 11:31 68	12/9/18 18:01 67	18/9/18 12:31 69	24/9/18 7:01 69
28/8/18 11:01 70 28/8/18 11:31 53	1/9/18 17:31 60 1/9/18 18:01 56	7/9/18 12:01 67 7/9/18 12:31 69	12/9/18 18:31 67 13/9/18 7:01 77	18/9/18 13:01 69 18/9/18 13:31 69	24/9/18 7:31 69 24/9/18 8:01 69
28/8/18 12:01 58	1/9/18 18:31 68	7/9/18 13:01 43	13/9/18 7:31 59	18/9/18 14:01 69	24/9/18 8:31 67
28/8/18 12:31 69 28/8/18 13:01 68	3/9/18 7:01 69 3/9/18 7:31 70	7/9/18 13:31 70 7/9/18 14:01 69	13/9/18 8:01 69 13/9/18 8:31 68	18/9/18 14:31 70 18/9/18 15:01 70	24/9/18 9:01 67 24/9/18 9:31 69
28/8/18 13:31 68	3/9/18 8:01 69	7/9/18 14:31 67	13/9/18 9:01 68	18/9/18 15:31 60	24/9/18 10:01 70
28/8/18 14:01 63 28/8/18 14:31 68	3/9/18 8:31 67 3/9/18 9:01 67	7/9/18 15:01 67 7/9/18 15:31 69	13/9/18 9:31 69 13/9/18 10:01 68	18/9/18 16:01 69 18/9/18 16:31 69	24/9/18 10:31 68 24/9/18 11:01 68
28/8/18 15:01 67	3/9/18 9:31 68	7/9/18 16:01 70	13/9/18 10:31 70	18/9/18 17:01 69	24/9/18 11:31 67
28/8/18 15:31 68	3/9/18 10:01 69 3/9/18 10:31 62	7/9/18 16:31 69	13/9/18 11:01 70 13/9/18 11:31 56	18/9/18 17:31 69 18/9/18 18:01 68	24/9/18 12:01 67 24/9/18 12:31 68
28/8/18 16:01 66 28/8/18 16:31 68	3/9/18 10:31 62 3/9/18 11:01 63	7/9/18 17:01 69 7/9/18 17:31 69	13/9/18 11:31 56 13/9/18 12:01 63	18/9/18 18:01 68 18/9/18 18:31 66	24/9/18 12:31 68 24/9/18 13:01 60
28/8/18 17:01 69	3/9/18 11:31 60	7/9/18 18:01 69	13/9/18 12:31 60	19/9/18 7:01 67	24/9/18 13:31 60 24/9/18 14:01 50
28/8/18 17:31 69 28/8/18 18:01 70	3/9/18 12:01 69 3/9/18 12:31 69	7/9/18 18:31 66 8/9/18 7:01 69	13/9/18 13:01 61 13/9/18 13:31 62	19/9/18 7:31 69 19/9/18 8:01 69	24/9/18 14:01 50 24/9/18 14:31 55
28/8/18 18:31 68	3/9/18 13:01 69	8/9/18 7:31 69	13/9/18 14:01 69	19/9/18 8:31 67	24/9/18 15:01 70
29/8/18 7:01 51 29/8/18 7:31 70	3/9/18 13:31 69 3/9/18 14:01 69	8/9/18 8:01 70 8/9/18 8:31 55	13/9/18 14:31 69 13/9/18 15:01 68	19/9/18 9:01 68 19/9/18 9:31 69	24/9/18 15:31 58 24/9/18 16:01 69
29/8/18 8:01 69	3/9/18 14:31 68	8/9/18 9:01 57	13/9/18 15:31 68 13/9/18 16:01 70	19/9/18 10:01 69	24/9/18 16:31 68 24/9/18 17:01 68
29/8/18 8:31 69 29/8/18 9:01 49	3/9/18 15:01 69 3/9/18 15:31 69	8/9/18 9:31 68 8/9/18 10:01 68	13/9/18 16:01 70 13/9/18 16:31 68	19/9/18 10:31 69 19/9/18 11:01 68	24/9/18 17:01 68 24/9/18 17:31 66
29/8/18 9:31 53	3/9/18 16:01 69	8/9/18 10:31 69	13/9/18 17:01 69	19/9/18 11:31 67	24/9/18 18:01 65
29/8/18 10:01 69 29/8/18 10:31 70	3/9/18 16:31 69 3/9/18 17:01 69	8/9/18 11:01 69 8/9/18 11:31 69	13/9/18 17:31 70 13/9/18 18:01 68	19/9/18 12:01 65 19/9/18 12:31 67	24/9/18 18:31 65 26/9/18 7:01 69
29/8/18 11:01 62	3/9/18 17:31 69	8/9/18 12:01 67	13/9/18 18:31 68	19/9/18 13:01 69	26/9/18 7:31 70
29/8/18 11:31 70 29/8/18 12:01 69	3/9/18 18:01 69 3/9/18 18:31 69	8/9/18 12:31 67 8/9/18 13:01 70	14/9/18 7:01 69 14/9/18 7:31 63	19/9/18 13:31 69 19/9/18 14:01 68	26/9/18 8:01 69 26/9/18 8:31 67
29/8/18 12:31 66	4/9/18 7:01 69	8/9/18 13:31 66	14/9/18 8:01 69	19/9/18 14:31 67	26/9/18 9:01 69
29/8/18 13:01 68 29/8/18 13:31 68	4/9/18 7:31 70 4/9/18 8:01 69	8/9/18 14:01 68 8/9/18 14:31 67	14/9/18 8:31 68 14/9/18 9:01 68	19/9/18 15:01 68 19/9/18 15:31 67	26/9/18 9:31 67 26/9/18 10:01 68
29/8/18 14:01 66	4/9/18 8:31 68	8/9/18 15:01 67	14/9/18 9:31 60	19/9/18 16:01 66	26/9/18 10:31 69
29/8/18 14:31 66 29/8/18 15:01 68	4/9/18 9:01 67 4/9/18 9:31 69	8/9/18 15:31 67 8/9/18 16:01 67	14/9/18 10:01 70 14/9/18 10:31 67	19/9/18 16:31 67 19/9/18 17:01 69	26/9/18 11:01 66 26/9/18 11:31 64
29/8/18 15:31 67	4/9/18 10:01 69	8/9/18 16:31 64	14/9/18 11:01 68	19/9/18 17:31 68	26/9/18 12:01 69
29/8/18 16:01 68 29/8/18 16:31 68	4/9/18 10:31 68 4/9/18 11:01 69	8/9/18 17:01 70 8/9/18 17:31 62	14/9/18 11:31 69 14/9/18 12:01 67	19/9/18 18:01 68 19/9/18 18:31 66	26/9/18 12:31 67 26/9/18 13:01 67
29/8/18 17:01 69	4/9/18 11:31 68	8/9/18 18:01 69	14/9/18 12:31 67	20/9/18 7:01 68	26/9/18 13:31 67
29/8/18 17:31 69 29/8/18 18:01 69	4/9/18 12:01 68 4/9/18 12:31 69	8/9/18 18:31 68 10/9/18 7:01 68	14/9/18 13:01 67 14/9/18 13:31 68	20/9/18 7:31 69 20/9/18 8:01 68	26/9/18 14:01 67 26/9/18 14:31 67
29/8/18 18:31 68	4/9/18 13:01 67	10/9/18 7:31 69	14/9/18 14:01 70	20/9/18 8:31 68	26/9/18 15:01 66
30/8/18 7:01 69 30/8/18 7:31 69	4/9/18 13:31 69 4/9/18 14:01 69	10/9/18 8:01 68 10/9/18 8:31 68	14/9/18 14:31 68 14/9/18 15:01 68	20/9/18 9:01 68 20/9/18 9:31 69	26/9/18 15:31 67 26/9/18 16:01 67
30/8/18 8:01 68	4/9/18 14:31 68	10/9/18 9:01 68	14/9/18 15:31 69	20/9/18 10:01 69	26/9/18 16:31 69
30/8/18 8:31 67	4/9/18 15:01 68	10/9/18 9:31 68	14/9/18 16:01 70	20/9/18 10:31 69	26/9/18 17:01 69 26/9/18 17:31 69
30/8/18 9:01 67 30/8/18 9:31 67	4/9/18 15:31 68 4/9/18 16:01 69	10/9/18 10:01 61 10/9/18 10:31 62	14/9/18 16:31 55 14/9/18 17:01 51	20/9/18 11:01 68 20/9/18 11:31 57	26/9/18 17:31 69 26/9/18 18:01 67
30/8/18 10:01 68	4/9/18 16:31 69	10/9/18 11:01 61	14/9/18 17:31 58	20/9/18 12:01 68	26/9/18 18:31 66
30/8/18 10:31 69 30/8/18 11:01 56	4/9/18 17:01 69 4/9/18 17:31 69	10/9/18 11:31 67 10/9/18 12:01 68	14/9/18 18:01 68 14/9/18 18:31 67	20/9/18 12:31 68 20/9/18 13:01 69	Normal Day 19:00-23:00,
30/8/18 11:31 69	4/9/18 18:01 69	10/9/18 12:31 69	15/9/18 7:01 69	20/9/18 13:31 69	Sunday & Holiday
30/8/18 12:01 68 30/8/18 12:31 69	4/9/18 18:31 69 5/9/18 7:01 68	10/9/18 13:01 57 10/9/18 13:31 57	15/9/18 7:31 69 15/9/18 8:01 70	20/9/18 14:01 69 20/9/18 14:31 67	07:00-23:00
30/8/18 13:01 53	5/9/18 7:31 69	10/9/18 14:01 59	15/9/18 8:31 69	20/9/18 15:01 67	27/8/18 19:01 64
30/8/18 13:31 70 30/8/18 14:01 70	5/9/18 8:01 69 5/9/18 8:31 58	10/9/18 14:31 67 10/9/18 15:01 68	15/9/18 9:01 68 15/9/18 9:31 68	20/9/18 15:31 68 20/9/18 16:01 68	27/8/18 19:06 64 27/8/18 19:11 64
30/8/18 14:31 68	5/9/18 9:01 70	10/9/18 15:31 68	15/9/18 10:01 68	20/9/18 16:31 69	27/8/18 19:16 63
30/8/18 15:01 69 30/8/18 15:31 38	5/9/18 9:31 69 5/9/18 10:01 69	10/9/18 16:01 68 10/9/18 16:31 68	15/9/18 10:31 68 15/9/18 11:01 67	20/9/18 17:01 66 20/9/18 17:31 66	27/8/18 19:21 63 27/8/18 19:26 63
30/8/18 16:01 69	5/9/18 10:31 68	10/9/18 17:01 69	15/9/18 11:31 67	20/9/18 18:01 66	27/8/18 19:31 63
30/8/18 16:31 69 30/8/18 17:01 69	5/9/18 11:01 69 5/9/18 11:31 53	10/9/18 17:31 69 10/9/18 18:01 64	15/9/18 12:01 68 15/9/18 12:31 66	20/9/18 18:31 65 21/9/18 7:01 68	27/8/18 19:36 66 27/8/18 19:41 65
30/8/18 17:01 69 30/8/18 17:31 69	5/9/18 11:31 53 5/9/18 12:01 69	10/9/18 18:01 64 10/9/18 18:31 69	15/9/18 12:31 66 15/9/18 13:01 66	21/9/18 7:01 68 21/9/18 7:31 69	27/8/18 19:41 65 27/8/18 19:46 65
30/8/18 18:01 69	5/9/18 12:31 69	11/9/18 7:01 70	15/9/18 13:31 66	21/9/18 8:01 68	27/8/18 19:51 65
30/8/18 18:31 69 31/8/18 7:01 70	5/9/18 13:01 69 5/9/18 13:31 69	11/9/18 7:31 69 11/9/18 8:01 69	15/9/18 14:01 68 15/9/18 14:31 67	21/9/18 8:31 67 21/9/18 9:01 67	27/8/18 19:56 64 27/8/18 20:01 64
31/8/18 7:31 69	5/9/18 14:01 69	11/9/18 8:31 70	15/9/18 15:01 67	21/9/18 9:31 68	27/8/18 20:06 63
31/8/18 8:01 68 31/8/18 8:31 67	5/9/18 14:31 68 5/9/18 15:01 67	11/9/18 9:01 61 11/9/18 9:31 57	15/9/18 15:31 68 15/9/18 16:01 69	21/9/18 10:01 70 21/9/18 10:31 70	27/8/18 20:11 63 27/8/18 20:16 62
31/8/18 9:01 66	5/9/18 15:31 68	11/9/18 10:01 53	15/9/18 16:31 70	21/9/18 11:01 54	27/8/18 20:21 61
31/8/18 9:31 67 31/8/18 10:01 68	5/9/18 16:01 68 5/9/18 16:31 67	11/9/18 10:31 35 11/9/18 11:01 70	15/9/18 17:01 69 15/9/18 17:31 69	21/9/18 11:31 56 21/9/18 12:01 69	27/8/18 20:26 63 27/8/18 20:31 64
31/8/18 10:31 70	5/9/18 17:01 68	11/9/18 11:31 68	15/9/18 18:01 69	21/9/18 12:31 69	27/8/18 20:36 63
31/8/18 11:01 70 31/8/18 11:31 69	5/9/18 17:31 69 5/9/18 18:01 69	11/9/18 12:01 66 11/9/18 12:31 68	15/9/18 18:31 69 17/9/18 7:01 67	21/9/18 13:01 69 21/9/18 13:31 67	27/8/18 20:41 64 27/8/18 20:46 63
31/8/18 12:01 67	5/9/18 18:31 69	11/9/18 13:01 69	17/9/18 7:31 67	21/9/18 14:01 67	27/8/18 20:51 64

<u>al-time Noise</u> /8/18 20:56 /8/18 21:01	67 67	29/8/18 22:01 65 29/8/18 22:06 64	1/9/18 19:06 1/9/18 19:11	65 67	2/9/18 12:11 2/9/18 12:16	67 67	2/9/18 21:16 2/9/18 21:21	63 63	4/9/18 22:21 4/9/18 22:26
/8/18 21:06 /8/18 21:11	65 66	29/8/18 22:11 65 29/8/18 22:16 65	1/9/18 19:16 1/9/18 19:21	65 66	2/9/18 12:21 2/9/18 12:26	68 70	2/9/18 21:26 2/9/18 21:31	64 61	4/9/18 22:31 4/9/18 22:36
/8/18 21:16	67	29/8/18 22:21 65	1/9/18 19:26	66	2/9/18 12:20	68	2/9/18 21:36	64	4/9/18 22:41
/8/18 21:21	67	29/8/18 22:26 64	1/9/18 19:31	66	2/9/18 12:36	68	2/9/18 21:41	66	4/9/18 22:46
/8/18 21:26 /8/18 21:31	66 66	29/8/18 22:31 65 29/8/18 22:36 65	1/9/18 19:36 1/9/18 19:41	66 66	2/9/18 12:41 2/9/18 12:46	68 69	2/9/18 21:46 2/9/18 21:51	61 63	4/9/18 22:51 4/9/18 22:56
/8/18 21:36	66	29/8/18 22:41 63	1/9/18 19:46	66	2/9/18 12:51	67	2/9/18 21:56	63	5/9/18 19:01
/8/18 21:41 /8/18 21:46	66 65	29/8/18 22:46 64 29/8/18 22:51 70	1/9/18 19:51 1/9/18 19:56	67 67	2/9/18 12:56 2/9/18 13:01	66 67	2/9/18 22:01 2/9/18 22:06	65 62	5/9/18 19:06 5/9/18 19:11
/8/18 21:51	65	29/8/18 22:56 64	1/9/18 20:01	66	2/9/18 13:06	67	2/9/18 22:11	63	5/9/18 19:16
8/18 21:56	67	30/8/18 19:01 65	1/9/18 20:06	68	2/9/18 13:11	67	2/9/18 22:16	63	5/9/18 19:21
8/18 22:01 8/18 22:06	66 66	30/8/18 19:06 66 30/8/18 19:11 65	1/9/18 20:11 1/9/18 20:16	66 65	2/9/18 13:16 2/9/18 13:21	66 65	2/9/18 22:21 2/9/18 22:26	63 63	5/9/18 19:26 5/9/18 19:31
8/18 22:11	67	30/8/18 19:16 65	1/9/18 20:21	67	2/9/18 13:26	68	2/9/18 22:31	61	5/9/18 19:36
8/18 22:16 8/18 22:21	67 67	30/8/18 19:21 65 30/8/18 19:26 65	1/9/18 20:26 1/9/18 20:31	65 65	2/9/18 13:31 2/9/18 13:36	65 65	2/9/18 22:36 2/9/18 22:41	63 66	5/9/18 19:41 5/9/18 19:46
8/18 22:26	69	30/8/18 19:31 64	1/9/18 20:36	66	2/9/18 13:41	66	2/9/18 22:46	62	5/9/18 19:51
8/18 22:31	67	30/8/18 19:36 65	1/9/18 20:41	65	2/9/18 13:46	68	2/9/18 22:51	58	5/9/18 19:56
8/18 22:36 8/18 22:41	67 68	30/8/18 19:41 64 30/8/18 19:46 65	1/9/18 20:46 1/9/18 20:51	66 66	2/9/18 13:51 2/9/18 13:56	66 65	2/9/18 22:56 3/9/18 19:01	59 67	5/9/18 20:01 5/9/18 20:06
8/18 22:46	67	30/8/18 19:51 67	1/9/18 20:56	64	2/9/18 14:01	65	3/9/18 19:06	64	5/9/18 20:11
8/18 22:51 8/18 22:56	67 67	30/8/18 19:56 65 30/8/18 20:01 65	1/9/18 21:01 1/9/18 21:06	66 64	2/9/18 14:06 2/9/18 14:11	66 66	3/9/18 19:11 3/9/18 19:16	65 65	5/9/18 20:16 5/9/18 20:21
8/18 19:01	65	30/8/18 20:06 67	1/9/18 21:11	64	2/9/18 14:16	65	3/9/18 19:21	65	5/9/18 20:26
8/18 19:06	66	30/8/18 20:11 66	1/9/18 21:16	64	2/9/18 14:21	68	3/9/18 19:26	64	5/9/18 20:31
8/18 19:11 8/18 19:16	66 49	30/8/18 20:16 65 30/8/18 20:21 65	1/9/18 21:21 1/9/18 21:26	64 64	2/9/18 14:26 2/9/18 14:31	66 66	3/9/18 19:31 3/9/18 19:36	66 66	5/9/18 20:36 5/9/18 20:41
8/18 19:21	49	30/8/18 20:26 66	1/9/18 21:31	65	2/9/18 14:36	66	3/9/18 19:41	65	5/9/18 20:46
8/18 19:26 8/18 19:31	66 60	30/8/18 20:31 64 30/8/18 20:36 62	1/9/18 21:36 1/9/18 21:41	66 65	2/9/18 14:41 2/9/18 14:46	67 65	3/9/18 19:46 3/9/18 19:51	65 68	5/9/18 20:51 5/9/18 20:56
8/18 19:36	62	30/8/18 20:41 64	1/9/18 21:46	66	2/9/18 14:51	64	3/9/18 19:56	64	5/9/18 21:01
8/18 19:41	65 66	30/8/18 20:46 64	1/9/18 21:51	66 67	2/9/18 14:56	63 62	3/9/18 20:01	64	5/9/18 21:06
8/18 19:46 8/18 19:51	66 66	30/8/18 20:51 64 30/8/18 20:56 64	1/9/18 21:56 1/9/18 22:01	67 66	2/9/18 15:01 2/9/18 15:06	63 64	3/9/18 20:06 3/9/18 20:11	66 65	5/9/18 21:11 5/9/18 21:16
8/18 19:56	66	30/8/18 21:01 65	1/9/18 22:06	66	2/9/18 15:11	66	3/9/18 20:16	66	5/9/18 21:21
/18 20:01 /18 20:06	64 65	30/8/18 21:06 64 30/8/18 21:11 65	1/9/18 22:11 1/9/18 22:16	67 66	2/9/18 15:16 2/9/18 15:21	65 66	3/9/18 20:21 3/9/18 20:26	65 64	5/9/18 21:26 5/9/18 21:31
8/18 20:11	66	30/8/18 21:16 65	1/9/18 22:21	65	2/9/18 15:26	65	3/9/18 20:31	65	5/9/18 21:36
8/18 20:16 8/18 20:21	65 65	30/8/18 21:21 64 30/8/18 21:26 64	1/9/18 22:26 1/9/18 22:31	66 67	2/9/18 15:31 2/9/18 15:36	64 67	3/9/18 20:36 3/9/18 20:41	67 63	5/9/18 21:41 5/9/18 21:46
3/18 20:26	64	30/8/18 21:31 64	1/9/18 22:36	66	2/9/18 15:41	64	3/9/18 20:46	63	5/9/18 21:51
8/18 20:31	66	30/8/18 21:36 64	1/9/18 22:41	66	2/9/18 15:46	64	3/9/18 20:51	63	5/9/18 21:56
3/18 20:36 3/18 20:41	65 65	30/8/18 21:41 64 30/8/18 21:46 64	1/9/18 22:46 1/9/18 22:51	66 68	2/9/18 15:51 2/9/18 15:56	63 64	3/9/18 20:56 3/9/18 21:01	67 62	5/9/18 22:01 5/9/18 22:06
8/18 20:46	65	30/8/18 21:51 65	1/9/18 22:56	65	2/9/18 16:01	65	3/9/18 21:06	64	5/9/18 22:11
3/18 20:51 3/18 20:56	65 65	30/8/18 21:56 64 30/8/18 22:01 65	2/9/18 7:01 2/9/18 7:06	59 58	2/9/18 16:06 2/9/18 16:11	63 63	3/9/18 21:11 3/9/18 21:16	61 64	5/9/18 22:16 5/9/18 22:21
3/18 21:01	63	30/8/18 22:06 63	2/9/18 7:11	73	2/9/18 16:16	62	3/9/18 21:21	62	5/9/18 22:26
8/18 21:06	65 65	30/8/18 22:11 64 30/8/18 22:16 64	2/9/18 7:16 2/9/18 7:21	58 61	2/9/18 16:21 2/9/18 16:26	64 66	3/9/18 21:26 3/9/18 21:31	62 66	5/9/18 22:31 5/9/18 22:36
3/18 21:11 3/18 21:16	65 65	30/8/18 22:21 64	2/9/18 7:26	60	2/9/18 16:20	64	3/9/18 21:36	63	5/9/18 22:41
8/18 21:21	65	30/8/18 22:26 65	2/9/18 7:31	63	2/9/18 16:36	66	3/9/18 21:41	65	5/9/18 22:46
3/18 21:26 3/18 21:31	66 64	30/8/18 22:31 65 30/8/18 22:36 64	2/9/18 7:36 2/9/18 7:41	63 59	2/9/18 16:41 2/9/18 16:46	65 64	3/9/18 21:46 3/9/18 21:51	61 61	5/9/18 22:51 5/9/18 22:56
8/18 21:36	65	30/8/18 22:41 63	2/9/18 7:46	62	2/9/18 16:51	66	3/9/18 21:56	62	6/9/18 19:01
8/18 21:41 8/18 21:46	65 66	30/8/18 22:46 64 30/8/18 22:51 63	2/9/18 7:51 2/9/18 7:56	63 64	2/9/18 16:56 2/9/18 17:01	66 65	3/9/18 22:01 3/9/18 22:06	62 57	6/9/18 19:06 6/9/18 19:11
8/18 21:51	65	30/8/18 22:56 63	2/9/18 8:01	66	2/9/18 17:06	64	3/9/18 22:11	61	6/9/18 19:16
8/18 21:56 8/18 22:01	66	31/8/18 19:01 57	2/9/18 8:06	65	2/9/18 17:11	65	3/9/18 22:16	64 65	6/9/18 19:21
3/18 22:01 3/18 22:06	65 66	31/8/18 19:06 66 31/8/18 19:11 66	2/9/18 8:11 2/9/18 8:16	65 64	2/9/18 17:16 2/9/18 17:21	65 64	3/9/18 22:21 3/9/18 22:26	65 63	6/9/18 19:26 6/9/18 19:31
8/18 22:11	66	31/8/18 19:16 63	2/9/18 8:21	64	2/9/18 17:26	61	3/9/18 22:31	62	6/9/18 19:36
3/18 22:16 3/18 22:21	65 66	31/8/18 19:21 66 31/8/18 19:26 66	2/9/18 8:26 2/9/18 8:31	62 64	2/9/18 17:31 2/9/18 17:36	66 63	3/9/18 22:36 3/9/18 22:41	62 63	6/9/18 19:41 6/9/18 19:46
8/18 22:26	65	31/8/18 19:31 66	2/9/18 8:36	64	2/9/18 17:41	53	3/9/18 22:46	63	6/9/18 19:51
3/18 22:31 3/18 22:36	64 64	31/8/18 19:36 66 31/8/18 19:41 65		66 69	2/9/18 17:46 2/9/18 17:51	64 66	3/9/18 22:51 3/9/18 22:56	62 63	6/9/18 19:56 6/9/18 20:01
8/18 22:41	65	31/8/18 19:46 65		69	2/9/18 17:56	66	4/9/18 19:01	64	6/9/18 20:06
8/18 22:46	64	31/8/18 19:51 66	2/9/18 8:56	67	2/9/18 18:01	67	4/9/18 19:06	63	6/9/18 20:11
3/18 22:51 3/18 22:56	65 63	31/8/18 19:56 65 31/8/18 20:01 66	2/9/18 9:01 2/9/18 9:06	66 67	2/9/18 18:06 2/9/18 18:11	66 66	4/9/18 19:11 4/9/18 19:16	63 64	6/9/18 20:16 6/9/18 20:21
/18 19:01	63	31/8/18 20:06 66	2/9/18 9:11	67	2/9/18 18:16	65	4/9/18 19:21	66	6/9/18 20:26
/18 19:06 /18 19:11	64 65	31/8/18 20:11 66 31/8/18 20:16 65	2/9/18 9:16 2/9/18 9:21	68 67	2/9/18 18:21 2/9/18 18:26	67 67	4/9/18 19:26 4/9/18 19:31	67 65	6/9/18 20:31 6/9/18 20:36
8/18 19:16	56	31/8/18 20:21 65	2/9/18 9:26	67	2/9/18 18:31	68	4/9/18 19:36	64	6/9/18 20:41
/18 19:21 /18 19:26	63 66	31/8/18 20:26 65 31/8/18 20:31 66	2/9/18 9:31 2/9/18 9:36	67 68	2/9/18 18:36 2/9/18 18:41	65 65	4/9/18 19:41 4/9/18 19:46	63 67	6/9/18 20:46 6/9/18 20:51
/18 19:20	67	31/8/18 20:36 65		67	2/9/18 18:46	66	4/9/18 19:51	63	6/9/18 20:56
/18 19:36	68	31/8/18 20:41 65		67	2/9/18 18:51	65	4/9/18 19:56	64	6/9/18 21:01
/18 19:41 /18 19:46	66 67	31/8/18 20:46 65 31/8/18 20:51 66	2/9/18 9:51 2/9/18 9:56	66 66	2/9/18 18:56 2/9/18 19:01	67 65	4/9/18 20:01 4/9/18 20:06	67 66	6/9/18 21:06 6/9/18 21:11
/18 19:51	65	31/8/18 20:56 64	2/9/18 10:01	67	2/9/18 19:06	65	4/9/18 20:11	63	6/9/18 21:16
/18 19:56 /18 20:01	65 67	31/8/18 21:01 63 31/8/18 21:06 64	2/9/18 10:06 2/9/18 10:11	66 66	2/9/18 19:11 2/9/18 19:16	66 64	4/9/18 20:16 4/9/18 20:21	67 65	6/9/18 21:21 6/9/18 21:26
/18 20:01	66	31/8/18 21:11 64	2/9/18 10:11	65	2/9/18 19:10	68	4/9/18 20:26	60	6/9/18 21:31
/18 20:11	66	31/8/18 21:16 65	2/9/18 10:21	67	2/9/18 19:26	65	4/9/18 20:31	62	6/9/18 21:36
/18 20:16 /18 20:21	64 65	31/8/18 21:21 65 31/8/18 21:26 64	2/9/18 10:26 2/9/18 10:31	67 67	2/9/18 19:31 2/9/18 19:36	67 65	4/9/18 20:36 4/9/18 20:41	64 62	6/9/18 21:41 6/9/18 21:46
/18 20:26	67	31/8/18 21:31 64	2/9/18 10:36	67	2/9/18 19:41	62	4/9/18 20:46	63	6/9/18 21:51
/18 20:31 /18 20:36	66 65	31/8/18 21:36 64 31/8/18 21:41 65	2/9/18 10:41 2/9/18 10:46	66 66	2/9/18 19:46 2/9/18 19:51	64 65	4/9/18 20:51 4/9/18 20:56	62 63	6/9/18 21:56 6/9/18 22:01
/18 20:30	65	31/8/18 21:46 66	2/9/18 10:51	66	2/9/18 19:56	64	4/9/18 21:01	63	6/9/18 22:06
/18 20:46	64	31/8/18 21:51 66		66	2/9/18 20:01	63	4/9/18 21:06	61	6/9/18 22:11
/18 20:51 /18 20:56	65 66	31/8/18 21:56 65 31/8/18 22:01 65	2/9/18 11:01 2/9/18 11:06	66 67	2/9/18 20:06 2/9/18 20:11	65 65	4/9/18 21:11 4/9/18 21:16	63 63	6/9/18 22:16 6/9/18 22:21
3/18 21:01	65	31/8/18 22:06 64	2/9/18 11:11	66	2/9/18 20:16	64	4/9/18 21:21	64	6/9/18 22:26
3/18 21:06	66 64	31/8/18 22:11 65 31/8/18 22:16 66	2/9/18 11:16 2/9/18 11:21	66 67	2/9/18 20:21 2/9/18 20:26	67 66	4/9/18 21:26 4/9/18 21:31	63 61	6/9/18 22:31 6/9/18 22:36
3/18 21:11 3/18 21:16	64 65	31/8/18 22:16 65	2/9/18 11:21	67 67	2/9/18 20:26 2/9/18 20:31	66 64	4/9/18 21:31 4/9/18 21:36	63	6/9/18 22:36
3/18 21:21	65	31/8/18 22:26 67	2/9/18 11:31	67	2/9/18 20:36	63	4/9/18 21:41	66	6/9/18 22:46
3/18 21:26 3/18 21:31	65 65	31/8/18 22:31 66 31/8/18 22:36 66	2/9/18 11:36 2/9/18 11:41	66 67	2/9/18 20:41 2/9/18 20:46	65 62	4/9/18 21:46 4/9/18 21:51	63 62	6/9/18 22:51 6/9/18 22:56
8/18 21:36	66	31/8/18 22:41 67	2/9/18 11:46	67	2/9/18 20:51	65	4/9/18 21:56	65	7/9/18 19:01
8/18 21:41 8/18 21:46	64 65	31/8/18 22:46 65 31/8/18 22:51 66	2/9/18 11:51 2/9/18 11:56	67 68	2/9/18 20:56 2/9/18 21:01	63 64	4/9/18 22:01 4/9/18 22:06	63 60	7/9/18 19:06
8/18 21:46 8/18 21:51	65 64	31/8/18 22:51 66 31/8/18 22:56 65	2/9/18 11:56 2/9/18 12:01	68 67	2/9/18 21:01 2/9/18 21:06	64 63	4/9/18 22:06 4/9/18 22:11	60 63	7/9/18 19:11 7/9/18 19:16
	64	1/9/18 19:01 66	2/9/18 12:06	66	2/9/18 21:11	62	4/9/18 22:16	61	7/9/18 19:21

Real-time Noise 7/9/18 19:26 7/9/18 19:31	53 63	9/9/18 8:31 9/9/18 8:36	66 66	5 Fan Memorial Scho 9/9/18 17:36 9/9/18 17:41	66 67	10/9/18 22:41 10/9/18 22:46	64 63	13/9/18 19:46 13/9/18 19:51	61 63	15/9/18 20:51 15/9/18 20:56	64 66
7/9/18 19:36	68	9/9/18 8:41	65	9/9/18 17:46	66	10/9/18 22:51	63	13/9/18 19:56	66	15/9/18 21:01	68
7/9/18 19:41 7/9/18 19:46	63 69	9/9/18 8:46 9/9/18 8:51	64 65	9/9/18 17:51 9/9/18 17:56	67 68	10/9/18 22:56 11/9/18 19:01	60 66	13/9/18 20:01 13/9/18 20:06	65 65	15/9/18 21:06 15/9/18 21:11	66 68
7/9/18 19:51	65	9/9/18 8:56	66	9/9/18 18:01	66	11/9/18 19:06	66	13/9/18 20:11	67	15/9/18 21:16	67
7/9/18 19:56	65	9/9/18 9:01	65	9/9/18 18:06	66	11/9/18 19:11	66	13/9/18 20:16	67	15/9/18 21:21	66
7/9/18 20:01 7/9/18 20:06	66 65	9/9/18 9:06 9/9/18 9:11	65 65	9/9/18 18:11 9/9/18 18:16	67 66	11/9/18 19:16 11/9/18 19:21	59 65	13/9/18 20:21 13/9/18 20:26	66 65	15/9/18 21:26 15/9/18 21:31	67 65
7/9/18 20:00	66	9/9/18 9:16	65	9/9/18 18:21	67	11/9/18 19:26	66	13/9/18 20:31	65	15/9/18 21:36	68
7/9/18 20:16	66	9/9/18 9:21	65	9/9/18 18:26	66	11/9/18 19:31	65	13/9/18 20:36	66	15/9/18 21:41	67
7/9/18 20:21 7/9/18 20:26	67 64	9/9/18 9:26 9/9/18 9:31	66 69	9/9/18 18:31 9/9/18 18:36	66 68	11/9/18 19:36 11/9/18 19:41	67 66	13/9/18 20:41 13/9/18 20:46	66 65	15/9/18 21:46 15/9/18 21:51	67 66
7/9/18 20:28	65	9/9/18 9:36	69 67	9/9/18 18:41	66	11/9/18 19:46	66	13/9/18 20:51	69	15/9/18 21:56	64
7/9/18 20:36	65	9/9/18 9:41	66	9/9/18 18:46	65	11/9/18 19:51	67	13/9/18 20:56	65	15/9/18 22:01	67
7/9/18 20:41 7/9/18 20:46	65 64	9/9/18 9:46 9/9/18 9:51	67 67	9/9/18 18:51 9/9/18 18:56	66 67	11/9/18 19:56 11/9/18 20:01	67 66	13/9/18 21:01 13/9/18 21:06	65 65	15/9/18 22:06 15/9/18 22:11	66 67
7/9/18 20:51	64	9/9/18 9:56	66	9/9/18 19:01	66	11/9/18 20:06	66	13/9/18 21:11	65	15/9/18 22:16	66
7/9/18 20:56	66	9/9/18 10:01	66	9/9/18 19:06	66	11/9/18 20:11	64	13/9/18 21:16	65	15/9/18 22:21	66
7/9/18 21:01 7/9/18 21:06	67 64	9/9/18 10:06 9/9/18 10:11	66 65	9/9/18 19:11 9/9/18 19:16	65 66	11/9/18 20:16 11/9/18 20:21	65 66	13/9/18 21:21 13/9/18 21:26	65 65	15/9/18 22:26 15/9/18 22:31	65 66
7/9/18 21:11	64	9/9/18 10:16	66	9/9/18 19:21	66	11/9/18 20:26	65	13/9/18 21:31	65	15/9/18 22:36	66
7/9/18 21:16	64	9/9/18 10:21	66	9/9/18 19:26	65	11/9/18 20:31	65	13/9/18 21:36	65	15/9/18 22:41	66
7/9/18 21:21 7/9/18 21:26	66 64	9/9/18 10:26 9/9/18 10:31	68 66	9/9/18 19:31 9/9/18 19:36	67 64	11/9/18 20:36 11/9/18 20:41	65 63	13/9/18 21:41 13/9/18 21:46	65 64	15/9/18 22:46 15/9/18 22:51	65 64
7/9/18 21:31	65	9/9/18 10:36	65	9/9/18 19:41	65	11/9/18 20:46	63	13/9/18 21:51	65	15/9/18 22:56	64
7/9/18 21:36	65	9/9/18 10:41	65	9/9/18 19:46	65	11/9/18 20:51	64	13/9/18 21:56	64	16/9/18 7:01	78
7/9/18 21:41 7/9/18 21:46	64 67	9/9/18 10:46 9/9/18 10:51	67 66	9/9/18 19:51 9/9/18 19:56	65 72	11/9/18 20:56 11/9/18 21:01	65 64	13/9/18 22:01 13/9/18 22:06	66 65	16/9/18 7:06 16/9/18 7:11	80 78
7/9/18 21:51	65	9/9/18 10:56	66	9/9/18 20:01	65	11/9/18 21:06	64	13/9/18 22:11	66	16/9/18 7:16	81
7/9/18 21:56	63 65	9/9/18 11:01	66 65	9/9/18 20:06	62 64	11/9/18 21:11	65 64	13/9/18 22:16	65 65	16/9/18 7:21	77
7/9/18 22:01 7/9/18 22:06	65	9/9/18 11:06 9/9/18 11:11	66	9/9/18 20:11 9/9/18 20:16	65	11/9/18 21:16 11/9/18 21:21	66	13/9/18 22:21 13/9/18 22:26	65 64	16/9/18 7:26 16/9/18 7:31	78 77
7/9/18 22:11	64	9/9/18 11:16	66	9/9/18 20:21	63	11/9/18 21:26	63	13/9/18 22:31	67	16/9/18 7:36	75
7/9/18 22:16	65	9/9/18 11:21	66	9/9/18 20:26	63	11/9/18 21:31	64	13/9/18 22:36 13/9/18 22:41	65 05	16/9/18 7:41 16/9/18 7:46	79
7/9/18 22:21 7/9/18 22:26	65 64	9/9/18 11:26 9/9/18 11:31	66 66	9/9/18 20:31 9/9/18 20:36	64 64	11/9/18 21:36 11/9/18 21:41	65 62	13/9/18 22:41	65 65	16/9/18 7:51	77 76
7/9/18 22:31	64	9/9/18 11:36	68	9/9/18 20:41	63	11/9/18 21:46	67	13/9/18 22:51	65	16/9/18 7:56	72
7/9/18 22:36 7/9/18 22:41	64 65	9/9/18 11:41 9/9/18 11:46	66 68	9/9/18 20:46 9/9/18 20:51	64 67	11/9/18 21:51 11/9/18 21:56	64 64	13/9/18 22:56 14/9/18 19:01	64 66	16/9/18 8:01 16/9/18 8:06	69 70
7/9/18 22:46	65	9/9/18 11:51	66	9/9/18 20:56	70	11/9/18 22:01	63	14/9/18 19:06	66	16/9/18 8:11	75
7/9/18 22:51	64	9/9/18 11:56	67	9/9/18 21:01	70	11/9/18 22:06	65	14/9/18 19:11	66	16/9/18 8:16	76
7/9/18 22:56 8/9/18 19:01	66 66	9/9/18 12:01 9/9/18 12:06	67 67	9/9/18 21:06 9/9/18 21:11	70 69	11/9/18 22:11 11/9/18 22:16	65 65	14/9/18 19:16 14/9/18 19:21	66 66	16/9/18 8:21 16/9/18 8:26	73 70
8/9/18 19:06	66	9/9/18 12:11	66	9/9/18 21:16	71	11/9/18 22:21	64	14/9/18 19:26	56	16/9/18 8:31	66
8/9/18 19:11	66	9/9/18 12:16	66	9/9/18 21:21	71	11/9/18 22:26	64	14/9/18 19:31	66	16/9/18 8:36	72
8/9/18 19:16 8/9/18 19:21	66 67	9/9/18 12:21 9/9/18 12:26	67 66	9/9/18 21:26 9/9/18 21:31	70 70	11/9/18 22:31 11/9/18 22:36	64 64	14/9/18 19:36 14/9/18 19:41	53 67	16/9/18 8:41 16/9/18 8:46	73 74
8/9/18 19:26	67	9/9/18 12:31	67	9/9/18 21:36	69	11/9/18 22:41	63	14/9/18 19:46	66	16/9/18 8:51	69
8/9/18 19:31	66	9/9/18 12:36	66	9/9/18 21:41	68	11/9/18 22:46	64	14/9/18 19:51	62	16/9/18 8:56	78
8/9/18 19:36 8/9/18 19:41	66 65	9/9/18 12:41 9/9/18 12:46	67 66	9/9/18 21:46 9/9/18 21:51	65 66	11/9/18 22:51 11/9/18 22:56	62 63	14/9/18 19:56 14/9/18 20:01	57 66	16/9/18 9:01 16/9/18 9:06	76 77
8/9/18 19:46	66	9/9/18 12:51	67	9/9/18 21:56	68	12/9/18 19:01	63	14/9/18 20:06	66	16/9/18 9:11	72
8/9/18 19:51	66	9/9/18 12:56	68	9/9/18 22:01	68	12/9/18 19:06	62	14/9/18 20:11	66	16/9/18 9:16	72
8/9/18 19:56 8/9/18 20:01	65 65	9/9/18 13:01 9/9/18 13:06	67 66	9/9/18 22:06 9/9/18 22:11	66 66	12/9/18 19:11 12/9/18 19:16	66 65	14/9/18 20:16 14/9/18 20:21	66 67	16/9/18 9:21 16/9/18 9:26	80 76
8/9/18 20:06	65	9/9/18 13:11	66	9/9/18 22:16	68	12/9/18 19:21	65	14/9/18 20:26	67	16/9/18 9:31	74
8/9/18 20:11 8/9/18 20:16	64 65	9/9/18 13:16 9/9/18 13:21	66 66	9/9/18 22:21 9/9/18 22:26	68 68	12/9/18 19:26 12/9/18 19:31	67 66	14/9/18 20:31 14/9/18 20:36	66 65	16/9/18 9:36 16/9/18 9:41	76 71
8/9/18 20:21	65	9/9/18 13:26	65	9/9/18 22:31	67	12/9/18 19:36	65	14/9/18 20:41	66	16/9/18 9:46	72
8/9/18 20:26	62	9/9/18 13:31	65	9/9/18 22:36	65	12/9/18 19:41	66	14/9/18 20:46	64	16/9/18 9:51	77
8/9/18 20:31 8/9/18 20:36	64 64	9/9/18 13:36 9/9/18 13:41	66 66	9/9/18 22:41 9/9/18 22:46	66 66	12/9/18 19:46 12/9/18 19:51	65 65	14/9/18 20:51 14/9/18 20:56	69 66	16/9/18 9:56 16/9/18 10:01	77 76
8/9/18 20:41	64	9/9/18 13:46	66	9/9/18 22:51	66	12/9/18 19:56	65	14/9/18 21:01	64	16/9/18 10:06	79
8/9/18 20:46	64	9/9/18 13:51 9/9/18 13:56	64	9/9/18 22:56	66	12/9/18 20:01	65	14/9/18 21:06	65 05	16/9/18 10:11	77
8/9/18 20:51 8/9/18 20:56	65 65	9/9/18 13:56	65 65	10/9/18 19:01 10/9/18 19:06	64 66	12/9/18 20:06 12/9/18 20:11	65 67	14/9/18 21:11 14/9/18 21:16	65 66	16/9/18 10:16 16/9/18 10:21	80 90
8/9/18 21:01	66	9/9/18 14:06	65	10/9/18 19:11	66	12/9/18 20:16	66	14/9/18 21:21	65	16/9/18 10:26	82
8/9/18 21:06 8/9/18 21:11	64	9/9/18 14:11 9/9/18 14:16	66	10/9/18 19:16 10/9/18 19:21	65 65	12/9/18 20:21 12/9/18 20:26	66 65	14/9/18 21:26 14/9/18 21:31	66 05	16/9/18 10:31	94 79
8/9/18 21:16	65 63	9/9/18 14:21	65 66	10/9/18 19:26	66	12/9/18 20:31	66	14/9/18 21:31	65 65	16/9/18 10:36 16/9/18 10:41	75
8/9/18 21:21	63	9/9/18 14:26	65	10/9/18 19:31	67	12/9/18 20:36	64	14/9/18 21:41	67	16/9/18 10:46	73
8/9/18 21:26 8/9/18 21:31	65 65	9/9/18 14:31 9/9/18 14:36	64 66	10/9/18 19:36 10/9/18 19:41	67 66	12/9/18 20:41 12/9/18 20:46	65 65	14/9/18 21:46 14/9/18 21:51	65 67	16/9/18 10:51 16/9/18 10:56	75 77
8/9/18 21:36	66	9/9/18 14:41	67	10/9/18 19:46	66	12/9/18 20:51	68	14/9/18 21:56	66	16/9/18 11:01	72
8/9/18 21:41	65	9/9/18 14:46	65	10/9/18 19:51	66	12/9/18 20:56	64	14/9/18 22:01	67	16/9/18 11:06	72
8/9/18 21:46 8/9/18 21:51	65 65	9/9/18 14:51 9/9/18 14:56	66 66	10/9/18 19:56 10/9/18 20:01	63 66	12/9/18 21:01 12/9/18 21:06	64 65	14/9/18 22:06 14/9/18 22:11	67 65	16/9/18 11:11 16/9/18 11:16	73 73
8/9/18 21:56	66	9/9/18 15:01	65	10/9/18 20:06	66	12/9/18 21:11	65	14/9/18 22:16	67	16/9/18 11:21	73
8/9/18 22:01	66	9/9/18 15:06	65	10/9/18 20:11	67	12/9/18 21:16	64	14/9/18 22:21	66	16/9/18 11:26	74
8/9/18 22:06 8/9/18 22:11	65 64	9/9/18 15:11 9/9/18 15:16	66 65	10/9/18 20:16 10/9/18 20:21	64 66	12/9/18 21:21 12/9/18 21:26	63 65	14/9/18 22:26 14/9/18 22:31	65 65	16/9/18 11:31 16/9/18 11:36	72 75
8/9/18 22:16	65	9/9/18 15:21	66	10/9/18 20:26	63	12/9/18 21:31	66	14/9/18 22:36	66	16/9/18 11:41	71
8/9/18 22:21	65	9/9/18 15:26	66	10/9/18 20:31	66	12/9/18 21:36	64	14/9/18 22:41	66	16/9/18 11:46	73
8/9/18 22:26 8/9/18 22:31	64 65	9/9/18 15:31 9/9/18 15:36	66 65	10/9/18 20:36 10/9/18 20:41	65 64	12/9/18 21:41 12/9/18 21:46	64 64	14/9/18 22:46 14/9/18 22:51	65 64	16/9/18 11:51 16/9/18 11:56	73 75
8/9/18 22:36	65	9/9/18 15:41	69	10/9/18 20:46	63	12/9/18 21:51	64	14/9/18 22:56	65	16/9/18 12:01	73
8/9/18 22:41	65	9/9/18 15:46	70	10/9/18 20:51	64	12/9/18 21:56	64	15/9/18 19:01	66	16/9/18 12:06	73
8/9/18 22:46 8/9/18 22:51	65 64	9/9/18 15:51 9/9/18 15:56	67 66	10/9/18 20:56 10/9/18 21:01	68 63	12/9/18 22:01 12/9/18 22:06	65 65	15/9/18 19:06 15/9/18 19:11	66 65	16/9/18 12:11 16/9/18 12:16	75 71
8/9/18 22:56	65	9/9/18 15:56	66	10/9/18 21:06	64	12/9/18 22:11	65	15/9/18 19:16	65	16/9/18 12:21	71
9/9/18 7:01	59	9/9/18 16:06	64	10/9/18 21:11	66	12/9/18 22:16	65	15/9/18 19:21	66 65	16/9/18 12:26	75
9/9/18 7:06 9/9/18 7:11	54 61	9/9/18 16:11 9/9/18 16:16	66 65	10/9/18 21:16 10/9/18 21:21	63 64	12/9/18 22:21 12/9/18 22:26	64 67	15/9/18 19:26 15/9/18 19:31	65 65	16/9/18 12:31 16/9/18 12:36	76 75
9/9/18 7:16	48	9/9/18 16:21	66	10/9/18 21:26	63	12/9/18 22:31	64	15/9/18 19:36	66	16/9/18 12:41	77
9/9/18 7:21	58	9/9/18 16:26	65 65	10/9/18 21:31	63	12/9/18 22:36	65 65	15/9/18 19:41	64	16/9/18 12:46	75
9/9/18 7:26 9/9/18 7:31	58 61	9/9/18 16:31 9/9/18 16:36	65 65	10/9/18 21:36 10/9/18 21:41	64 65	12/9/18 22:41 12/9/18 22:46	65 63	15/9/18 19:46 15/9/18 19:51	64 63	16/9/18 12:51 16/9/18 12:56	75 72
9/9/18 7:36	62	9/9/18 16:41	65	10/9/18 21:46	62	12/9/18 22:51	64	15/9/18 19:56	64	16/9/18 13:01	73
9/9/18 7:41	60	9/9/18 16:46	65	10/9/18 21:51	64	12/9/18 22:56	64	15/9/18 20:01	64	16/9/18 13:06	69
9/9/18 7:46 9/9/18 7:51	61 63	9/9/18 16:51 9/9/18 16:56	65 65	10/9/18 21:56 10/9/18 22:01	63 65	13/9/18 19:01 13/9/18 19:06	66 66	15/9/18 20:06 15/9/18 20:11	64 67	16/9/18 13:11 16/9/18 13:16	71 70
9/9/18 7:56	65	9/9/18 17:01	66	10/9/18 22:06	62	13/9/18 19:11	65	15/9/18 20:16	63	16/9/18 13:21	70
9/9/18 8:01	62	9/9/18 17:06	65	10/9/18 22:11	63	13/9/18 19:16	63	15/9/18 20:21	64	16/9/18 13:26	69
9/9/18 8:06 9/9/18 8:11	62 63	9/9/18 17:11 9/9/18 17:16	66 65	10/9/18 22:16 10/9/18 22:21	61 64	13/9/18 19:21 13/9/18 19:26	66 66	15/9/18 20:26 15/9/18 20:31	63 65	16/9/18 13:31 16/9/18 13:36	71 68
9/9/18 8:16	68	9/9/18 17:21	66	10/9/18 22:26	65	13/9/18 19:31	66	15/9/18 20:36	64	16/9/18 13:41	75
9/9/18 8:21	65	9/9/18 17:26	65 65	10/9/18 22:31	66	13/9/18 19:36	63	15/9/18 20:41	64	16/9/18 13:46	68
9/9/18 8:26	63	9/9/18 17:31	65	10/9/18 22:36	64	13/9/18 19:41	66	15/9/18 20:46	64	16/9/18 13:51	67

Real-time Noise Data 16/9/18 13:56 68 16/9/18 14:01 69 16/9/18 14:00 60	RTN3 (Po Leung Kuk Yu Lee Mo 17/9/18 19:01 66 17/9/18 19:06 64 17/9/18 19:06 64	19/9/18 20:06 65 19/9/18 20:11 64	21/9/18 21:11 65 21/9/18 21:16 65	23/9/18 10:16 65 23/9/18 10:21 65	23/9/18 19:21 65 23/9/18 19:26 65
16/9/18 14:06 66 16/9/18 14:11 67	17/9/18 19:11 64 17/9/18 19:16 64	19/9/18 20:16 65 19/9/18 20:21 64	21/9/18 21:21 64 21/9/18 21:26 66	23/9/18 10:26 65 23/9/18 10:31 65	23/9/18 19:31 65 23/9/18 19:36 65
16/9/18 14:16 64	17/9/18 19:21 63	19/9/18 20:26 65	21/9/18 21:31 65	23/9/18 10:36 65	23/9/18 19:41 64
16/9/18 14:21 65 16/9/18 14:26 64	17/9/18 19:26 64 17/9/18 19:31 63	19/9/18 20:31 64 19/9/18 20:36 65	21/9/18 21:36 64 21/9/18 21:41 65	23/9/18 10:41 65 23/9/18 10:46 66	23/9/18 19:46 65 23/9/18 19:51 63
16/9/18 14:26 64 16/9/18 14:31 64	17/9/18 19:31 63 17/9/18 19:36 63	19/9/18 20:36 65 19/9/18 20:41 64	21/9/18 21:41 65 21/9/18 21:46 64	23/9/18 10:46 66 23/9/18 10:51 65	23/9/18 19:51 63 23/9/18 19:56 64
16/9/18 14:36 63	17/9/18 19:41 63	19/9/18 20:46 64	21/9/18 21:51 65	23/9/18 10:56 63	23/9/18 20:01 63
16/9/18 14:41 64 16/9/18 14:46 64	17/9/18 19:46 63 17/9/18 19:51 63	19/9/18 20:51 64 19/9/18 20:56 64	21/9/18 21:56 65 21/9/18 22:01 64	23/9/18 11:01 65 23/9/18 11:06 65	23/9/18 20:06 64 23/9/18 20:11 64
16/9/18 14:51 60	17/9/18 19:56 63	19/9/18 21:01 65	21/9/18 22:06 64	23/9/18 11:11 66	23/9/18 20:16 66
16/9/18 14:56 60	17/9/18 20:01 61	19/9/18 21:06 64	21/9/18 22:11 66	23/9/18 11:16 65	23/9/18 20:21 63
16/9/18 15:01 58 16/9/18 15:06 51	17/9/18 20:06 63 17/9/18 20:11 62	19/9/18 21:11 64 19/9/18 21:16 62	21/9/18 22:16 65 21/9/18 22:21 65	23/9/18 11:21 64 23/9/18 11:26 65	23/9/18 20:26 65 23/9/18 20:31 64
16/9/18 15:11 66	17/9/18 20:16 62	19/9/18 21:21 63	21/9/18 22:26 65	23/9/18 11:31 63	23/9/18 20:36 64
16/9/18 15:16 66 16/9/18 15:21 66	17/9/18 20:21 62 17/9/18 20:26 63	19/9/18 21:26 65 19/9/18 21:31 62	21/9/18 22:31 65 21/9/18 22:36 65	23/9/18 11:36 61 23/9/18 11:41 64	23/9/18 20:41 64 23/9/18 20:46 64
16/9/18 15:26 66	17/9/18 20:31 62	19/9/18 21:36 63	21/9/18 22:41 64	23/9/18 11:46 64	23/9/18 20:51 63
16/9/18 15:31 65	17/9/18 20:36 62 17/9/18 20:41 63	19/9/18 21:41 65 19/9/18 21:46 67	21/9/18 22:46 63 21/9/18 22:51 65	23/9/18 11:51 66 23/9/18 11:56 65	23/9/18 20:56 64
16/9/18 15:36 65 16/9/18 15:41 64	17/9/18 20:41 63 17/9/18 20:46 63	19/9/18 21:46 67 19/9/18 21:51 64	21/9/18 22:51 65 21/9/18 22:56 64	23/9/18 11:56 65 23/9/18 12:01 65	23/9/18 21:01 64 23/9/18 21:06 64
16/9/18 15:46 65	17/9/18 20:51 62	19/9/18 21:56 62	22/9/18 19:01 66	23/9/18 12:06 65	23/9/18 21:11 65
16/9/18 15:51 65 16/9/18 15:56 66	17/9/18 20:56 61 17/9/18 21:01 60	19/9/18 22:01 64 19/9/18 22:06 61	22/9/18 19:06 66 22/9/18 19:11 63	23/9/18 12:11 66 23/9/18 12:16 65	23/9/18 21:16 64 23/9/18 21:21 64
16/9/18 16:01 66	17/9/18 21:06 66	19/9/18 22:11 66	22/9/18 19:16 68	23/9/18 12:21 66	23/9/18 21:26 64
16/9/18 16:06 66 16/9/18 16:11 65	17/9/18 21:11 62 17/9/18 21:16 62	19/9/18 22:16 63 19/9/18 22:21 63	22/9/18 19:21 66 22/9/18 19:26 66	23/9/18 12:26 65 23/9/18 12:31 66	23/9/18 21:31 65 23/9/18 21:36 64
16/9/18 16:16 65	17/9/18 21:21 63	19/9/18 22:26 64	22/9/18 19:31 66	23/9/18 12:36 67	23/9/18 21:41 64
16/9/18 16:21 55 16/9/18 16:26 63	17/9/18 21:26 62 17/9/18 21:31 61	19/9/18 22:31 63 19/9/18 22:36 63	22/9/18 19:36 67 22/9/18 19:41 66	23/9/18 12:41 66 23/9/18 12:46 66	23/9/18 21:46 64 23/9/18 21:51 67
16/9/18 16:26 63 16/9/18 16:31 63	17/9/18 21:31 61 17/9/18 21:36 61	19/9/18 22:36 63 19/9/18 22:41 65	22/9/18 19:41 66 22/9/18 19:46 65	23/9/18 12:46 66 23/9/18 12:51 66	23/9/18 21:51 67 23/9/18 21:56 66
16/9/18 16:36 48	17/9/18 21:41 61	19/9/18 22:46 62	22/9/18 19:51 66	23/9/18 12:56 68	23/9/18 22:01 63
16/9/18 16:41 62 16/9/18 16:46 66	17/9/18 21:46 63 17/9/18 21:51 59	19/9/18 22:51 63 19/9/18 22:56 62	22/9/18 19:56 64 22/9/18 20:01 65	23/9/18 13:01 65 23/9/18 13:06 66	23/9/18 22:06 65 23/9/18 22:11 64
16/9/18 16:51 64	17/9/18 21:56 61	20/9/18 19:01 65	22/9/18 20:06 67	23/9/18 13:11 66	23/9/18 22:16 63
16/9/18 16:56 63 16/9/18 17:01 63	17/9/18 22:01 59 17/9/18 22:06 63	20/9/18 19:06 66 20/9/18 19:11 65	22/9/18 20:11 64 22/9/18 20:16 67	23/9/18 13:16 64 23/9/18 13:21 65	23/9/18 22:21 64 23/9/18 22:26 63
16/9/18 17:06 62	17/9/18 22:11 59	20/9/18 19:16 66	22/9/18 20:21 65	23/9/18 13:26 65	23/9/18 22:31 65
16/9/18 17:11 62 16/9/18 17:16 66	17/9/18 22:16 63 17/9/18 22:21 62	20/9/18 19:21 66 20/9/18 19:26 66	22/9/18 20:26 64 22/9/18 20:31 66	23/9/18 13:31 66 23/9/18 13:36 65	23/9/18 22:36 65 23/9/18 22:41 64
16/9/18 17:21 61	17/9/18 22:26 61	20/9/18 19:31 66	22/9/18 20:36 65	23/9/18 13:41 66	23/9/18 22:46 62
16/9/18 17:26 65 16/9/18 17:31 63	17/9/18 22:31 61 17/9/18 22:36 61	20/9/18 19:36 66 20/9/18 19:41 45	22/9/18 20:41 65 22/9/18 20:46 63	23/9/18 13:46 64 23/9/18 13:51 65	23/9/18 22:51 61 23/9/18 22:56 66
16/9/18 17:31 63 16/9/18 17:36 60	17/9/18 22:41 61	20/9/18 19:46 62	22/9/18 20:51 65	23/9/18 13:56 65	24/9/18 19:01 60
16/9/18 17:41 61	17/9/18 22:46 61	20/9/18 19:51 63	22/9/18 20:56 66	23/9/18 14:01 65	24/9/18 19:06 66
16/9/18 17:46 62 16/9/18 17:51 60	17/9/18 22:51 63 17/9/18 22:56 57	20/9/18 19:56 67 20/9/18 20:01 64	22/9/18 21:01 64 22/9/18 21:06 64	23/9/18 14:06 65 23/9/18 14:11 64	24/9/18 19:11 57 24/9/18 19:16 65
16/9/18 17:56 63	18/9/18 19:01 66	20/9/18 20:06 63	22/9/18 21:11 64	23/9/18 14:16 65	24/9/18 19:21 65
16/9/18 18:01 60 16/9/18 18:06 60	18/9/18 19:06 66 18/9/18 19:11 65	20/9/18 20:11 64 20/9/18 20:16 65	22/9/18 21:16 64 22/9/18 21:21 65	23/9/18 14:21 65 23/9/18 14:26 64	24/9/18 19:26 65 24/9/18 19:31 64
16/9/18 18:11 61	18/9/18 19:16 66	20/9/18 20:21 63	22/9/18 21:26 63	23/9/18 14:31 65	24/9/18 19:36 65
16/9/18 18:16 61 16/9/18 18:21 60	18/9/18 19:21 66 18/9/18 19:26 63	20/9/18 20:26 65 20/9/18 20:31 65	22/9/18 21:31 64 22/9/18 21:36 65	23/9/18 14:36 64 23/9/18 14:41 64	24/9/18 19:41 65 24/9/18 19:46 65
16/9/18 18:26 61	18/9/18 19:31 58	20/9/18 20:36 65	22/9/18 21:41 65	23/9/18 14:46 63	24/9/18 19:51 64
16/9/18 18:31 62 16/9/18 18:36 61	18/9/18 19:36 65 18/9/18 19:41 66	20/9/18 20:41 64 20/9/18 20:46 64	22/9/18 21:46 64 22/9/18 21:51 64	23/9/18 14:51 64 23/9/18 14:56 65	24/9/18 19:56 63 24/9/18 20:01 64
16/9/18 18:41 60	18/9/18 19:46 65	20/9/18 20:51 62	22/9/18 21:56 64	23/9/18 15:01 65	24/9/18 20:06 64
16/9/18 18:46 60 16/9/18 18:51 61	18/9/18 19:51 65 18/9/18 19:56 65	20/9/18 20:56 61 20/9/18 21:01 61	22/9/18 22:01 64 22/9/18 22:06 65	23/9/18 15:06 64 23/9/18 15:11 63	24/9/18 20:11 65 24/9/18 20:16 65
16/9/18 18:56 62	18/9/18 20:01 65	20/9/18 21:06 63	22/9/18 22:11 64	23/9/18 15:16 63	24/9/18 20:21 66
16/9/18 19:01 60 16/9/18 19:06 61	18/9/18 20:06 65 18/9/18 20:11 66	20/9/18 21:11 61 20/9/18 21:16 62	22/9/18 22:16 64 22/9/18 22:21 64	23/9/18 15:21 63 23/9/18 15:26 63	24/9/18 20:26 65 24/9/18 20:31 64
16/9/18 19:11 61	18/9/18 20:16 67	20/9/18 21:21 64	22/9/18 22:26 65	23/9/18 15:31 63	24/9/18 20:36 64
16/9/18 19:16 60 16/9/18 19:21 60	18/9/18 20:21 65 18/9/18 20:26 65	20/9/18 21:26 64 20/9/18 21:31 65	22/9/18 22:31 66 22/9/18 22:36 64	23/9/18 15:36 63 23/9/18 15:41 63	24/9/18 20:41 62 24/9/18 20:46 65
16/9/18 19:26 61	18/9/18 20:20 65	20/9/18 21:36 65	22/9/18 22:41 65	23/9/18 15:46 63	24/9/18 20:51 64
16/9/18 19:31 62	18/9/18 20:36 65	20/9/18 21:41 64	22/9/18 22:46 62 22/9/18 22:51 64	23/9/18 15:51 63	24/9/18 20:56 63
16/9/18 19:36 63 16/9/18 19:41 63	18/9/18 20:41 63 18/9/18 20:46 64	20/9/18 21:46 61 20/9/18 21:51 62	22/9/18 22:51 64 22/9/18 22:56 65	23/9/18 15:56 64 23/9/18 16:01 63	24/9/18 21:01 64 24/9/18 21:06 65
16/9/18 19:46 62	18/9/18 20:51 67	20/9/18 21:56 64	23/9/18 7:01 46	23/9/18 16:06 63	24/9/18 21:11 63
16/9/18 19:51 55 16/9/18 19:56 64	18/9/18 20:56 66 18/9/18 21:01 68	20/9/18 22:01 63 20/9/18 22:06 65	23/9/18 7:06 53 23/9/18 7:11 65	23/9/18 16:11 63 23/9/18 16:16 63	24/9/18 21:16 64 24/9/18 21:21 64
16/9/18 20:01 66	18/9/18 21:06 64	20/9/18 22:11 61	23/9/18 7:16 52	23/9/18 16:21 64	24/9/18 21:26 65
16/9/18 20:06 64 16/9/18 20:11 64	18/9/18 21:11 65 18/9/18 21:16 65	20/9/18 22:16 63 20/9/18 22:21 63	23/9/18 7:21 60 23/9/18 7:26 60	23/9/18 16:26 67 23/9/18 16:31 67	24/9/18 21:31 65 24/9/18 21:36 66
16/9/18 20:16 63	18/9/18 21:21 64	20/9/18 22:26 65	23/9/18 7:31 64	23/9/18 16:36 66	24/9/18 21:41 65
16/9/18 20:21 64	18/9/18 21:26 66	20/9/18 22:31 63	23/9/18 7:36 62	23/9/18 16:41 66	24/9/18 21:46 66
16/9/18 20:26 65 16/9/18 20:31 64	18/9/18 21:31 65 18/9/18 21:36 65	20/9/18 22:36 62 20/9/18 22:41 63	23/9/18 7:41 61 23/9/18 7:46 63	23/9/18 16:46 66 23/9/18 16:51 68	24/9/18 21:51 66 24/9/18 21:56 64
16/9/18 20:36 64	18/9/18 21:41 65	20/9/18 22:46 64	23/9/18 7:51 62	23/9/18 16:56 67	24/9/18 22:01 66
16/9/18 20:41 64 16/9/18 20:46 63	18/9/18 21:46 65 18/9/18 21:51 65	20/9/18 22:51 63 20/9/18 22:56 61	23/9/18 7:56 63 23/9/18 8:01 62	23/9/18 17:01 66 23/9/18 17:06 66	24/9/18 22:06 66 24/9/18 22:11 66
16/9/18 20:51 63	18/9/18 21:56 64	21/9/18 19:01 65	23/9/18 8:06 63	23/9/18 17:11 66	24/9/18 22:16 67
16/9/18 20:56 63 16/9/18 21:01 64	18/9/18 22:01 66 18/9/18 22:06 65	21/9/18 19:06 66 21/9/18 19:11 66	23/9/18 8:11 63 23/9/18 8:16 63	23/9/18 17:16 66 23/9/18 17:21 66	24/9/18 22:21 65 24/9/18 22:26 65
16/9/18 21:06 62	18/9/18 22:11 64	21/9/18 19:16 65	23/9/18 8:21 65	23/9/18 17:26 66	24/9/18 22:31 67
16/9/18 21:11 62 16/9/18 21:16 63	18/9/18 22:16 63 18/9/18 22:21 64	21/9/18 19:21 66 21/9/18 19:26 64	23/9/18 8:26 64 23/9/18 8:31 62	23/9/18 17:31 64 23/9/18 17:36 64	24/9/18 22:36 65 24/9/18 22:41 66
16/9/18 21:21 63	18/9/18 22:26 64	21/9/18 19:31 66	23/9/18 8:36 63	23/9/18 17:41 64	24/9/18 22:46 66
16/9/18 21:26 62 16/9/18 21:31 63	18/9/18 22:31 63 18/9/18 22:36 63	21/9/18 19:36 66 21/9/18 19:41 45	23/9/18 8:41 65 23/9/18 8:46 64	23/9/18 17:46 63 23/9/18 17:51 62	24/9/18 22:51 66 24/9/18 22:56 66
16/9/18 21:31 63 16/9/18 21:36 65	18/9/18 22:36 63 18/9/18 22:41 66	21/9/18 19:41 45 21/9/18 19:46 61	23/9/18 8:46 64 23/9/18 8:51 64	23/9/18 17:51 62 23/9/18 17:56 63	24/9/18 22:56 66 25/9/18 7:01 63
16/9/18 21:41 62	18/9/18 22:46 64	21/9/18 19:51 64	23/9/18 8:56 65	23/9/18 18:01 64	25/9/18 7:06 64
16/9/18 21:46 62 16/9/18 21:51 63	18/9/18 22:51 64 18/9/18 22:56 63	21/9/18 19:56 63 21/9/18 20:01 63	23/9/18 9:01 64 23/9/18 9:06 62	23/9/18 18:06 65 23/9/18 18:11 64	25/9/18 7:11 64 25/9/18 7:16 57
16/9/18 21:56 63	19/9/18 19:01 58	21/9/18 20:06 64	23/9/18 9:11 64	23/9/18 18:16 64	25/9/18 7:21 60
16/9/18 22:01 63 16/9/18 22:06 63	19/9/18 19:06 66 19/9/18 19:11 66	21/9/18 20:11 65 21/9/18 20:16 64	23/9/18 9:16 65 23/9/18 9:21 64	23/9/18 18:21 64 23/9/18 18:26 65	25/9/18 7:26 60 25/9/18 7:31 62
16/9/18 22:11 62	19/9/18 19:16 66	21/9/18 20:21 64	23/9/18 9:26 65	23/9/18 18:31 65	25/9/18 7:36 62
16/9/18 22:16 62 16/9/18 22:21 63	19/9/18 19:21 66 19/9/18 19:26 66	21/9/18 20:26 63 21/9/18 20:31 65	23/9/18 9:31 66 23/9/18 9:36 66	23/9/18 18:36 64 23/9/18 18:41 64	25/9/18 7:41 65 25/9/18 7:46 64
16/9/18 22:26 62	19/9/18 19:31 66	21/9/18 20:36 64	23/9/18 9:41 66	23/9/18 18:46 65	25/9/18 7:51 61
16/9/18 22:31 62 16/9/18 22:36 60	19/9/18 19:36 66 19/9/18 19:41 65	21/9/18 20:41 63 21/9/18 20:46 64	23/9/18 9:46 65 23/9/18 9:51 65	23/9/18 18:51 65 23/9/18 18:56 65	25/9/18 7:56 62 25/9/18 8:01 60
16/9/18 22:41 61	19/9/18 19:46 65	21/9/18 20:51 66	23/9/18 9:56 66	23/9/18 19:01 66	25/9/18 8:06 63
16/9/18 22:46 61 16/9/18 22:51 61	19/9/18 19:51 63 19/9/18 19:56 64	21/9/18 20:56 64 21/9/18 21:01 63	23/9/18 10:01 65 23/9/18 10:06 65	23/9/18 19:06 66 23/9/18 19:11 64	25/9/18 8:11 61 25/9/18 8:16 68
16/9/18 22:56 61	19/9/18 20:01 64	21/9/18 21:06 64	23/9/18 10:06 65	23/9/18 19:11 64 23/9/18 19:16 63	25/9/18 8:16 68
			· ·	•	

Real-time Noise Data 25/9/18 8:26 63	RTN3 (Po Leung Kuk Yu Lee Mo 25/9/18 17:31 64	Fan Memorial School) 26/9/18 22:36 65	28/8/18 0:26 66	29/8/18 1:31 63	30/8/18 2:36 63
25/9/18 8:31 63	25/9/18 17:36 65	26/9/18 22:41 64	28/8/18 0:31 63	29/8/18 1:36 63	30/8/18 2:41 63
25/9/18 8:36 64 25/9/18 8:41 66	25/9/18 17:41 65 25/9/18 17:46 66	26/9/18 22:46 63 26/9/18 22:51 63	28/8/18 0:36 63 28/8/18 0:41 64	29/8/18 1:41 63 29/8/18 1:46 63	30/8/18 2:46 63 30/8/18 2:51 63
25/9/18 8:46 65	25/9/18 17:51 65	26/9/18 22:56 63	28/8/18 0:46 69	29/8/18 1:51 63	30/8/18 2:56 63
25/9/18 8:51 64	25/9/18 17:56 65	Night times 02:00 07:00	28/8/18 0:51 72	29/8/18 1:56 63	30/8/18 3:01 62
25/9/18 8:56 65 25/9/18 9:01 64	25/9/18 18:01 63 25/9/18 18:06 63	Night time: 23:00-07:00	28/8/18 0:56 71 28/8/18 1:01 68	29/8/18 2:01 63 29/8/18 2:06 48	30/8/18 3:06 61 30/8/18 3:11 62
25/9/18 9:06 67	25/9/18 18:11 66	27/8/18 0:01 68	28/8/18 1:06 68	29/8/18 2:11 43	30/8/18 3:16 62
25/9/18 9:11 63 25/9/18 9:16 66	25/9/18 18:16 65 25/9/18 18:21 65	27/8/18 0:06 66 27/8/18 0:11 67	28/8/18 1:11 68 28/8/18 1:16 65	29/8/18 2:16 62 29/8/18 2:21 62	30/8/18 3:21 62 30/8/18 3:26 60
25/9/18 9:21 65	25/9/18 18:26 64	27/8/18 0:16 66	28/8/18 1:21 65	29/8/18 2:26 63	30/8/18 3:31 61
25/9/18 9:26 66	25/9/18 18:31 64	27/8/18 0:21 67	28/8/18 1:26 66	29/8/18 2:31 62	30/8/18 3:36 61
25/9/18 9:31 65 25/9/18 9:36 65	25/9/18 18:36 64 25/9/18 18:41 66	27/8/18 0:26 66 27/8/18 0:31 65	28/8/18 1:31 65 28/8/18 1:36 62	29/8/18 2:36 62 29/8/18 2:41 62	30/8/18 3:41 63 30/8/18 3:46 62
25/9/18 9:41 66	25/9/18 18:46 67	27/8/18 0:36 65	28/8/18 1:41 63	29/8/18 2:46 61	30/8/18 3:51 62
25/9/18 9:46 66 25/9/18 9:51 66	25/9/18 18:51 65	27/8/18 0:41 65	28/8/18 1:46 58	29/8/18 2:51 61	30/8/18 3:56 61 30/8/18 4:01 60
25/9/18 9:51 66 25/9/18 9:56 65	25/9/18 18:56 65 25/9/18 19:01 63	27/8/18 0:46 63 27/8/18 0:51 62	28/8/18 1:51 62 28/8/18 1:56 60	29/8/18 2:56 62 29/8/18 3:01 62	30/8/18 4:01 60 30/8/18 4:06 62
25/9/18 10:01 64	25/9/18 19:06 64	27/8/18 0:56 61	28/8/18 2:01 60	29/8/18 3:06 63	30/8/18 4:11 62
25/9/18 10:06 64 25/9/18 10:11 66	25/9/18 19:11 63 25/9/18 19:16 64	27/8/18 1:01 60 27/8/18 1:06 60	28/8/18 2:06 56 28/8/18 2:11 58	29/8/18 3:11 62 29/8/18 3:16 61	30/8/18 4:16 61 30/8/18 4:21 60
25/9/18 10:16 64	25/9/18 19:21 63	27/8/18 1:11 58	28/8/18 2:16 56	29/8/18 3:21 61	30/8/18 4:26 60
25/9/18 10:21 66 25/9/18 10:26 66	25/9/18 19:26 63 25/9/18 19:31 64	27/8/18 1:16 58 27/8/18 1:21 59	28/8/18 2:21 54 28/8/18 2:26 58	29/8/18 3:26 62 29/8/18 3:31 61	30/8/18 4:31 61 30/8/18 4:36 46
25/9/18 10:31 66	25/9/18 19:36 63	27/8/18 1:26 58	28/8/18 2:31 55	29/8/18 3:36 60	30/8/18 4:41 49
25/9/18 10:36 66	25/9/18 19:41 65	27/8/18 1:31 56	28/8/18 2:36 63	29/8/18 3:41 60	30/8/18 4:46 63
25/9/18 10:41 66 25/9/18 10:46 66	25/9/18 19:46 65 25/9/18 19:51 63	27/8/18 1:36 58 27/8/18 1:41 63	28/8/18 2:41 50 28/8/18 2:46 58	29/8/18 3:46 42 29/8/18 3:51 62	30/8/18 4:51 53 30/8/18 4:56 62
25/9/18 10:51 66	25/9/18 19:56 64	27/8/18 1:46 53	28/8/18 2:51 63	29/8/18 3:56 61	30/8/18 5:01 48
25/9/18 10:56 65 25/9/18 11:01 66	25/9/18 20:01 62 25/9/18 20:06 62	27/8/18 1:51 57 27/8/18 1:56 52	28/8/18 2:56 63 28/8/18 3:01 62	29/8/18 4:01 61 29/8/18 4:06 62	30/8/18 5:06 54 30/8/18 5:11 43
25/9/18 11:06 65	25/9/18 20:11 63	27/8/18 2:01 56	28/8/18 3:06 67	29/8/18 4:11 62	30/8/18 5:16 56
25/9/18 11:11 66 25/9/18 11:16 65	25/9/18 20:16 63 25/9/18 20:21 63	27/8/18 2:06 54 27/8/18 2:11 63	28/8/18 3:11 67 28/8/18 3:16 61	29/8/18 4:16 61 29/8/18 4:21 62	30/8/18 5:21 59 30/8/18 5:26 60
25/9/18 11:21 64	25/9/18 20:26 64	27/8/18 2:16 62	28/8/18 3:21 53	29/8/18 4:26 62	30/8/18 5:31 57
25/9/18 11:26 65 25/9/18 11:31 65	25/9/18 20:31 64 25/9/18 20:36 63	27/8/18 2:21 63 27/8/18 2:26 63	28/8/18 3:26 59 28/8/18 3:31 62	29/8/18 4:31 61	30/8/18 5:36 58
25/9/18 11:31 65 25/9/18 11:36 66	25/9/18 20:36 63 25/9/18 20:41 63	27/8/18 2:26 63 27/8/18 2:31 63	28/8/18 3:31 62 28/8/18 3:36 58	29/8/18 4:36 63 29/8/18 4:41 62	30/8/18 5:41 57 30/8/18 5:46 62
25/9/18 11:41 66	25/9/18 20:46 62	27/8/18 2:36 62	28/8/18 3:41 57	29/8/18 4:46 54	30/8/18 5:51 61
25/9/18 11:46 66 25/9/18 11:51 66	25/9/18 20:51 60 25/9/18 20:56 63	27/8/18 2:41 63 27/8/18 2:46 60	28/8/18 3:46 62 28/8/18 3:51 63	29/8/18 4:51 63 29/8/18 4:56 53	30/8/18 5:56 62 30/8/18 6:01 60
25/9/18 11:56 66	25/9/18 21:01 64	27/8/18 2:51 62	28/8/18 3:56 63	29/8/18 5:01 62	30/8/18 6:06 64
25/9/18 12:01 66 25/9/18 12:06 66	25/9/18 21:06 64 25/9/18 21:11 64	27/8/18 2:56 61 27/8/18 3:01 62	28/8/18 4:01 62 28/8/18 4:06 62	29/8/18 5:06 58 29/8/18 5:11 59	30/8/18 6:11 63 30/8/18 6:16 65
25/9/18 12:11 64	25/9/18 21:16 65	27/8/18 3:06 62	28/8/18 4:11 61	29/8/18 5:16 53	30/8/18 6:21 66
25/9/18 12:16 66 25/9/18 12:21 66	25/9/18 21:21 64 25/9/18 21:26 64	27/8/18 3:11 63 27/8/18 3:16 62	28/8/18 4:16 61 28/8/18 4:21 58	29/8/18 5:21 56 29/8/18 5:26 60	30/8/18 6:26 67 30/8/18 6:31 66
25/9/18 12:26 67	25/9/18 21:31 62	27/8/18 3:21 62	28/8/18 4:26 57	29/8/18 5:31 56	30/8/18 6:36 67
25/9/18 12:31 66 25/9/18 12:36 65	25/9/18 21:36 64 25/9/18 21:41 64	27/8/18 3:26 63 27/8/18 3:31 62	28/8/18 4:31 61 28/8/18 4:36 63	29/8/18 5:36 63 29/8/18 5:41 60	30/8/18 6:41 67 30/8/18 6:46 67
25/9/18 12:41 65	25/9/18 21:46 65	27/8/18 3:36 63	28/8/18 4:41 63	29/8/18 5:46 62	30/8/18 6:51 67
25/9/18 12:46 66 25/9/18 12:51 66	25/9/18 21:51 64 25/9/18 21:56 64	27/8/18 3:41 62 27/8/18 3:46 59	28/8/18 4:46 54 28/8/18 4:51 52	29/8/18 5:51 61 29/8/18 5:56 62	30/8/18 6:56 67 30/8/18 23:01 67
25/9/18 12:56 65	25/9/18 22:01 64	27/8/18 3:51 62	28/8/18 4:56 63	29/8/18 6:01 62	30/8/18 23:06 67
25/9/18 13:01 68 25/9/18 13:06 67	25/9/18 22:06 62 25/9/18 22:11 66	27/8/18 3:56 62 27/8/18 4:01 62	28/8/18 5:01 63 28/8/18 5:06 56	29/8/18 6:06 63 29/8/18 6:11 64	30/8/18 23:11 68 30/8/18 23:16 67
25/9/18 13:11 64	25/9/18 22:16 64	27/8/18 4:06 61	28/8/18 5:11 60	29/8/18 6:16 64	30/8/18 23:21 68
25/9/18 13:16 65	25/9/18 22:21 64	27/8/18 4:11 61	28/8/18 5:16 61 28/8/18 5:21 59	29/8/18 6:21 65	30/8/18 23:26 67
25/9/18 13:21 66 25/9/18 13:26 65	25/9/18 22:26 66 25/9/18 22:31 62	27/8/18 4:16 61 27/8/18 4:21 63	28/8/18 5:21 59 28/8/18 5:26 58	29/8/18 6:26 66 29/8/18 6:31 66	30/8/18 23:31 68 30/8/18 23:36 66
25/9/18 13:31 64	25/9/18 22:36 64	27/8/18 4:26 45	28/8/18 5:31 59	29/8/18 6:36 66	30/8/18 23:41 66
25/9/18 13:36 65 25/9/18 13:41 64	25/9/18 22:41 66 25/9/18 22:46 61	27/8/18 4:31 62 27/8/18 4:36 60	28/8/18 5:36 62 28/8/18 5:41 52	29/8/18 6:41 67 29/8/18 6:46 67	30/8/18 23:46 65 30/8/18 23:51 66
25/9/18 13:46 65	25/9/18 22:51 61	27/8/18 4:41 63	28/8/18 5:46 60	29/8/18 6:51 68	30/8/18 23:56 65
25/9/18 13:51 65 25/9/18 13:56 65	25/9/18 22:56 63 26/9/18 19:01 66	27/8/18 4:46 52 27/8/18 4:51 62	28/8/18 5:51 62 28/8/18 5:56 61	29/8/18 6:56 68 29/8/18 23:01 67	31/8/18 0:01 65 31/8/18 0:06 64
25/9/18 14:01 66	26/9/18 19:06 65	27/8/18 4:56 62	28/8/18 6:01 62	29/8/18 23:06 69	31/8/18 0:11 64
25/9/18 14:06 65 25/9/18 14:11 67	26/9/18 19:11 64 26/9/18 19:16 64	27/8/18 5:01 62 27/8/18 5:06 63	28/8/18 6:06 65 28/8/18 6:11 64	29/8/18 23:11 67 29/8/18 23:16 67	31/8/18 0:16 64 31/8/18 0:21 63
25/9/18 14:16 64	26/9/18 19:21 64	27/8/18 5:11 55	28/8/18 6:16 65	29/8/18 23:21 67	31/8/18 0:26 67
25/9/18 14:21 65 25/9/18 14:26 65	26/9/18 19:26 65	27/8/18 5:16 63	28/8/18 6:21 66	29/8/18 23:26 67	31/8/18 0:31 68
25/9/18 14:26 65 25/9/18 14:31 65	26/9/18 19:31 64 26/9/18 19:36 65	27/8/18 5:21 58 27/8/18 5:26 57	28/8/18 6:26 66 28/8/18 6:31 66	29/8/18 23:31 66 29/8/18 23:36 65	31/8/18 0:36 67 31/8/18 0:41 64
25/9/18 14:36 66	26/9/18 19:41 64	27/8/18 5:31 57	28/8/18 6:36 68	29/8/18 23:41 66	31/8/18 0:46 62
25/9/18 14:41 66 25/9/18 14:46 67	26/9/18 19:46 64 26/9/18 19:51 65	27/8/18 5:36 59 27/8/18 5:41 59	28/8/18 6:41 68 28/8/18 6:46 68	29/8/18 23:46 66 29/8/18 23:51 67	31/8/18 0:51 61 31/8/18 0:56 60
25/9/18 14:51 65	26/9/18 19:56 66	27/8/18 5:46 61	28/8/18 6:51 68	29/8/18 23:56 66	31/8/18 1:01 61
25/9/18 14:56 67 25/9/18 15:01 66	26/9/18 20:01 65 26/9/18 20:06 64	27/8/18 5:51 62 27/8/18 5:56 61	28/8/18 6:56 68 28/8/18 23:01 67	30/8/18 0:01 65 30/8/18 0:06 65	31/8/18 1:06 60 31/8/18 1:11 66
25/9/18 15:06 65	26/9/18 20:11 65	27/8/18 6:01 63	28/8/18 23:06 68	30/8/18 0:11 65	31/8/18 1:16 68
25/9/18 15:11 65	26/9/18 20:16 66	27/8/18 6:06 63	28/8/18 23:11 67	30/8/18 0:16 66	31/8/18 1:21 68
25/9/18 15:16 67 25/9/18 15:21 66	26/9/18 20:21 64 26/9/18 20:26 65	27/8/18 6:11 66 27/8/18 6:16 72	28/8/18 23:16 66 28/8/18 23:21 67	30/8/18 0:21 64 30/8/18 0:26 65	31/8/18 1:26 68 31/8/18 1:31 72
25/9/18 15:26 66	26/9/18 20:31 66	27/8/18 6:21 72	28/8/18 23:26 66	30/8/18 0:31 65	31/8/18 1:36 74
25/9/18 15:31 68 25/9/18 15:36 65	26/9/18 20:36 64 26/9/18 20:41 64	27/8/18 6:26 66 27/8/18 6:31 66	28/8/18 23:31 65 28/8/18 23:36 66	30/8/18 0:36 64 30/8/18 0:41 62	31/8/18 1:41 72 31/8/18 1:46 63
25/9/18 15:41 67	26/9/18 20:46 64	27/8/18 6:36 66	28/8/18 23:41 66	30/8/18 0:46 58	31/8/18 1:51 61
25/9/18 15:46 65 25/9/18 15:51 68	26/9/18 20:51 62 26/9/18 20:56 62	27/8/18 6:41 67 27/8/18 6:46 68	28/8/18 23:46 65 28/8/18 23:51 66	30/8/18 0:51 59 30/8/18 0:56 59	31/8/18 1:56 59 31/8/18 2:01 72
25/9/18 15:56 65	26/9/18 21:01 63	27/8/18 6:51 68	28/8/18 23:56 65	30/8/18 1:01 57	31/8/18 2:06 68
25/9/18 16:01 66	26/9/18 21:06 63	27/8/18 6:56 68	29/8/18 0:01 65	30/8/18 1:06 57	31/8/18 2:11 70
25/9/18 16:06 66 25/9/18 16:11 66	26/9/18 21:11 65 26/9/18 21:16 65	27/8/18 23:01 68 27/8/18 23:06 67	29/8/18 0:06 65 29/8/18 0:11 65	30/8/18 1:11 57 30/8/18 1:16 59	31/8/18 2:16 62 31/8/18 2:21 66
25/9/18 16:16 66	26/9/18 21:21 64	27/8/18 23:11 67	29/8/18 0:16 65	30/8/18 1:21 59	31/8/18 2:26 67
25/9/18 16:21 66 25/9/18 16:26 65	26/9/18 21:26 63 26/9/18 21:31 63	27/8/18 23:16 67 27/8/18 23:21 67	29/8/18 0:21 65 29/8/18 0:26 66	30/8/18 1:26 56 30/8/18 1:31 55	31/8/18 2:31 66 31/8/18 2:36 65
25/9/18 16:31 65	26/9/18 21:36 64	27/8/18 23:26 67	29/8/18 0:31 64	30/8/18 1:36 58	31/8/18 2:41 55
25/9/18 16:36 64 25/9/18 16:41 66	26/9/18 21:41 64 26/9/18 21:46 62	27/8/18 23:31 69 27/8/18 23:36 66	29/8/18 0:36 64 29/8/18 0:41 64	30/8/18 1:41 42 30/8/18 1:46 63	31/8/18 2:46 51 31/8/18 2:51 50
25/9/18 16:46 65	26/9/18 21:51 64	27/8/18 23:41 68	29/8/18 0:46 63	30/8/18 1:51 59	31/8/18 2:56 63
25/9/18 16:51 64 25/9/18 16:56 65	26/9/18 21:56 62 26/9/18 22:01 63	27/8/18 23:46 66 27/8/18 23:51 66	29/8/18 0:51 62 29/8/18 0:56 62	30/8/18 1:56 51 30/8/18 2:01 45	31/8/18 3:01 52 31/8/18 3:06 63
25/9/18 16:56 65 25/9/18 17:01 67	26/9/18 22:01 63 26/9/18 22:06 67	27/8/18 23:51 66 27/8/18 23:56 66	29/8/18 0:56 62 29/8/18 1:01 58	30/8/18 2:01 45 30/8/18 2:06 63	31/8/18 3:06 63 31/8/18 3:11 62
25/9/18 17:06 66	26/9/18 22:11 63	28/8/18 0:01 65	29/8/18 1:06 59	30/8/18 2:11 63	31/8/18 3:16 62
25/9/18 17:11 65 25/9/18 17:16 65	26/9/18 22:16 63 26/9/18 22:21 62	28/8/18 0:06 65 28/8/18 0:11 66	29/8/18 1:11 56 29/8/18 1:16 57	30/8/18 2:16 63 30/8/18 2:21 42	31/8/18 3:21 63 31/8/18 3:26 61
25/9/18 17:21 65	26/9/18 22:26 63	28/8/18 0:16 65	29/8/18 1:21 56	30/8/18 2:26 63	31/8/18 3:31 62
25/9/18 17:26 65	26/9/18 22:31 62	28/8/18 0:21 66	29/8/18 1:26 55	30/8/18 2:31 63	31/8/18 3:36 47

/8/18 3:41 /8/18 3:46	62 62	1/9/18 4:46 59 1/9/18 4:51 60	e Mo Fan Memorial School) 2/9/18 5:51 62 2/9/18 5:56 61	3/9/18 6:56 69 3/9/18 23:01 65	5/9/18 0:01 65 5/9/18 0:06 64	6/9/18 1:06 6/9/18 1:11
/8/18 3:51 /8/18 3:56	62 37	1/9/18 4:56 60 1/9/18 5:01 61	2/9/18 6:01 64 2/9/18 6:06 66	3/9/18 23:06 66 3/9/18 23:11 65	5/9/18 0:11 65 5/9/18 0:16 63	6/9/18 1:16 6/9/18 1:21
/8/18 4:01	62	1/9/18 5:06 60	2/9/18 6:11 63	3/9/18 23:16 66	5/9/18 0:21 65	6/9/18 1:26
/8/18 4:06	62	1/9/18 5:11 62	2/9/18 6:16 69	3/9/18 23:21 66	5/9/18 0:26 66	6/9/18 1:31
/8/18 4:11 /8/18 4:16	62 40	1/9/18 5:16 59 1/9/18 5:21 59	2/9/18 6:21 68 2/9/18 6:26 64	3/9/18 23:26 65 3/9/18 23:31 66	5/9/18 0:31 64 5/9/18 0:36 63	6/9/18 1:36 6/9/18 1:41
/8/18 4:21	63	1/9/18 5:26 63	2/9/18 6:31 65	3/9/18 23:36 67	5/9/18 0:41 64	6/9/18 1:46
/8/18 4:26	63	1/9/18 5:31 62	2/9/18 6:36 64	3/9/18 23:41 64	5/9/18 0:46 62	6/9/18 1:51
/8/18 4:31 /8/18 4:36	48 63	1/9/18 5:36 61 1/9/18 5:41 61	2/9/18 6:41 66 2/9/18 6:46 67	3/9/18 23:46 65 3/9/18 23:51 64	5/9/18 0:51 62 5/9/18 0:56 62	6/9/18 1:56 6/9/18 2:01
/8/18 4:41	55	1/9/18 5:46 64	2/9/18 6:51 66	3/9/18 23:56 64	5/9/18 1:01 62	6/9/18 2:06
8/18 4:46	63	1/9/18 5:51 63	2/9/18 6:56 68	4/9/18 0:01 62	5/9/18 1:06 62	6/9/18 2:11
8/18 4:51 8/18 4:56	63 63	1/9/18 5:56 62 1/9/18 6:01 63	2/9/18 23:01 65 2/9/18 23:06 64	4/9/18 0:06 63 4/9/18 0:11 65	5/9/18 1:11 65 5/9/18 1:16 60	6/9/18 2:16 6/9/18 2:21
8/18 5:01	63	1/9/18 6:06 63	2/9/18 23:11 65	4/9/18 0:16 64	5/9/18 1:21 57	6/9/18 2:26
8/18 5:06	51	1/9/18 6:11 63	2/9/18 23:16 65	4/9/18 0:21 63	5/9/18 1:26 59	6/9/18 2:31
/8/18 5:11 /8/18 5:16	52 62	1/9/18 6:16 63 1/9/18 6:21 66	2/9/18 23:21 64 2/9/18 23:26 66	4/9/18 0:26 63 4/9/18 0:31 63	5/9/18 1:31 57 5/9/18 1:36 58	6/9/18 2:36 6/9/18 2:41
8/18 5:21	53	1/9/18 6:26 67	2/9/18 23:31 64	4/9/18 0:36 65	5/9/18 1:41 54	6/9/18 2:46
8/18 5:26	57	1/9/18 6:31 68	2/9/18 23:36 64	4/9/18 0:41 64	5/9/18 1:46 58	6/9/18 2:51
8/18 5:31 8/18 5:36	55 59	1/9/18 6:36 68 1/9/18 6:41 67	2/9/18 23:41 64 2/9/18 23:46 64	4/9/18 0:46 63 4/9/18 0:51 60	5/9/18 1:51 60 5/9/18 1:56 59	6/9/18 2:56 6/9/18 3:01
8/18 5:41	59	1/9/18 6:46 66	2/9/18 23:51 63	4/9/18 0:56 61	5/9/18 2:01 50	6/9/18 3:06
8/18 5:46	60	1/9/18 6:51 67	2/9/18 23:56 66	4/9/18 1:01 60	5/9/18 2:06 55	6/9/18 3:11
8/18 5:51 8/18 5:56	58 61	1/9/18 6:56 67 1/9/18 23:01 68	3/9/18 0:01 62 3/9/18 0:06 67	4/9/18 1:06 59 4/9/18 1:11 59	5/9/18 2:11 49 5/9/18 2:16 53	6/9/18 3:16 6/9/18 3:21
8/18 6:01	64	1/9/18 23:06 67	3/9/18 0:08 67	4/9/18 1:16 58	5/9/18 2:21 55	6/9/18 3:26
8/18 6:06	63	1/9/18 23:11 67	3/9/18 0:16 61	4/9/18 1:21 50	5/9/18 2:26 60	6/9/18 3:31
8/18 6:11	63	1/9/18 23:16 67	3/9/18 0:21 63	4/9/18 1:26 55	5/9/18 2:31 56	6/9/18 3:36
8/18 6:16 8/18 6:21	64 64	1/9/18 23:21 68 1/9/18 23:26 67	3/9/18 0:26 63 3/9/18 0:31 62	4/9/18 1:31 56 4/9/18 1:36 60	5/9/18 2:36 63 5/9/18 2:41 63	6/9/18 3:41 6/9/18 3:46
8/18 6:26	66	1/9/18 23:31 67	3/9/18 0:36 62	4/9/18 1:41 63	5/9/18 2:46 62	6/9/18 3:51
8/18 6:31	65	1/9/18 23:36 67	3/9/18 0:41 63	4/9/18 1:46 49	5/9/18 2:51 62	6/9/18 3:56
3/18 6:36 3/18 6:41	66 66	1/9/18 23:41 68 1/9/18 23:46 67	3/9/18 0:46 59 3/9/18 0:51 61	4/9/18 1:51 63 4/9/18 1:56 50	5/9/18 2:56 62 5/9/18 3:01 49	6/9/18 4:01 6/9/18 4:06
8/18 6:46	67	1/9/18 23:51 68	3/9/18 0:56 61	4/9/18 2:01 51	5/9/18 3:06 62	6/9/18 4:11
8/18 6:51	68	1/9/18 23:56 67	3/9/18 1:01 62	4/9/18 2:06 63	5/9/18 3:11 63	6/9/18 4:16
3/18 6:56 3/18 23:01	68 68	2/9/18 0:01 66 2/9/18 0:06 66	3/9/18 1:06 60 3/9/18 1:11 61	4/9/18 2:11 63 4/9/18 2:16 63	5/9/18 3:16 61 5/9/18 3:21 63	6/9/18 4:21 6/9/18 4:26
3/18 23:06	67	2/9/18 0:11 67	3/9/18 1:16 56	4/9/18 2:21 63	5/9/18 3:26 62	6/9/18 4:31
8/18 23:11	67	2/9/18 0:16 67	3/9/18 1:21 64	4/9/18 2:26 62	5/9/18 3:31 55	6/9/18 4:36
3/18 23:16 3/18 23:21	67 69	2/9/18 0:21 66 2/9/18 0:26 66	3/9/18 1:26 60 3/9/18 1:31 59	4/9/18 2:31 63 4/9/18 2:36 62	5/9/18 3:36 63 5/9/18 3:41 63	6/9/18 4:41 6/9/18 4:46
3/18 23:26	67	2/9/18 0:31 66	3/9/18 1:36 57	4/9/18 2:41 63	5/9/18 3:46 62	6/9/18 4:51
8/18 23:31	67	2/9/18 0:36 66	3/9/18 1:41 56	4/9/18 2:46 62	5/9/18 3:51 62	6/9/18 4:56
8/18 23:36	67 67	2/9/18 0:41 66	3/9/18 1:46 56	4/9/18 2:51 63	5/9/18 3:56 63	6/9/18 5:01
3/18 23:41 3/18 23:46	67 67	2/9/18 0:46 66 2/9/18 0:51 65	3/9/18 1:51 54 3/9/18 1:56 51	4/9/18 2:56 55 4/9/18 3:01 63	5/9/18 4:01 62 5/9/18 4:06 63	6/9/18 5:06 6/9/18 5:11
3/18 23:51	67	2/9/18 0:56 65	3/9/18 2:01 62	4/9/18 3:06 55	5/9/18 4:11 61	6/9/18 5:16
8/18 23:56	67 67	2/9/18 1:01 64 2/9/18 1:06 65	3/9/18 2:06 37 3/9/18 2:11 55	4/9/18 3:11 63	5/9/18 4:16 63	6/9/18 5:21
/18 0:01 /18 0:06	66	2/9/18 1:06 65 2/9/18 1:11 64	3/9/18 2:11 55 3/9/18 2:16 54	4/9/18 3:16 48 4/9/18 3:21 63	5/9/18 4:21 63 5/9/18 4:26 53	6/9/18 5:26 6/9/18 5:31
/18 0:11	67	2/9/18 1:16 65	3/9/18 2:21 59	4/9/18 3:26 62	5/9/18 4:31 62	6/9/18 5:36
/18 0:16	67	2/9/18 1:21 64	3/9/18 2:26 56	4/9/18 3:31 55	5/9/18 4:36 62	6/9/18 5:41
/18 0:21 /18 0:26	67 66	2/9/18 1:26 64 2/9/18 1:31 63	3/9/18 2:31 55 3/9/18 2:36 62	4/9/18 3:36 63 4/9/18 3:41 46	5/9/18 4:41 62 5/9/18 4:46 44	6/9/18 5:46 6/9/18 5:51
/18 0:31	66	2/9/18 1:36 63	3/9/18 2:41 47	4/9/18 3:46 62	5/9/18 4:51 62	6/9/18 5:56
/18 0:36	65	2/9/18 1:41 64	3/9/18 2:46 61	4/9/18 3:51 62	5/9/18 4:56 53	6/9/18 6:01
/18 0:41 /18 0:46	66 65	2/9/18 1:46 62 2/9/18 1:51 66	3/9/18 2:51 53 3/9/18 2:56 61	4/9/18 3:56 63 4/9/18 4:01 63	5/9/18 5:01 63 5/9/18 5:06 48	6/9/18 6:06 6/9/18 6:11
/18 0:51	65	2/9/18 1:56 64	3/9/18 3:01 62	4/9/18 4:06 46	5/9/18 5:11 55	6/9/18 6:16
/18 0:56	66	2/9/18 2:01 61	3/9/18 3:06 50	4/9/18 4:11 62	5/9/18 5:16 54	6/9/18 6:21
/18 1:01 /18 1:06	66 65	2/9/18 2:06 63 2/9/18 2:11 63	3/9/18 3:11 62 3/9/18 3:16 62	4/9/18 4:16 62 4/9/18 4:21 63	5/9/18 5:21 57 5/9/18 5:26 59	6/9/18 6:26 6/9/18 6:31
/18 1:11	66	2/9/18 2:16 63	3/9/18 3:21 60	4/9/18 4:26 52	5/9/18 5:31 59	6/9/18 6:36
/18 1:16	66	2/9/18 2:21 63	3/9/18 3:26 63	4/9/18 4:31 62	5/9/18 5:36 58	6/9/18 6:41
/18 1:21 /18 1:26	65 65	2/9/18 2:26 63 2/9/18 2:31 61	3/9/18 3:31 53 3/9/18 3:36 62	4/9/18 4:36 62 4/9/18 4:41 63	5/9/18 5:41 61 5/9/18 5:46 60	6/9/18 6:46 6/9/18 6:51
18 1:31	64	2/9/18 2:36 65	3/9/18 3:41 62	4/9/18 4:46 62	5/9/18 5:51 61	6/9/18 6:56
18 1:36	65	2/9/18 2:41 63	3/9/18 3:46 63	4/9/18 4:51 63	5/9/18 5:56 61	6/9/18 23:01
18 1:41 18 1:46	65 66	2/9/18 2:46 61 2/9/18 2:51 62	3/9/18 3:51 60 3/9/18 3:56 62	4/9/18 4:56 63 4/9/18 5:01 62	5/9/18 6:01 62 5/9/18 6:06 63	6/9/18 23:06 6/9/18 23:11
18 1:51	64	2/9/18 2:56 61	3/9/18 4:01 61	4/9/18 5:06 50	5/9/18 6:11 64	6/9/18 23:16
18 1:56	65	2/9/18 3:01 63	3/9/18 4:06 62	4/9/18 5:11 63	5/9/18 6:16 65	6/9/18 23:21
18 2:01 18 2:06	63 64	2/9/18 3:06 62 2/9/18 3:11 60	3/9/18 4:11 62 3/9/18 4:16 62	4/9/18 5:16 59 4/9/18 5:21 45	5/9/18 6:21 66 5/9/18 6:26 66	6/9/18 23:26 6/9/18 23:31
18 2:11	64 64	2/9/18 3:16 59	3/9/18 4:16 62	4/9/18 5:26 55	5/9/18 6:31 66	6/9/18 23:36
18 2:16	64	2/9/18 3:21 61	3/9/18 4:26 61	4/9/18 5:31 58	5/9/18 6:36 67	6/9/18 23:41
18 2:21 18 2:26	64 64	2/9/18 3:26 61 2/9/18 3:31 62	3/9/18 4:31 62 3/9/18 4:36 63	4/9/18 5:36 61 4/9/18 5:41 59	5/9/18 6:41 68 5/9/18 6:46 67	6/9/18 23:46 6/9/18 23:51
18 2:31	63	2/9/18 3:36 61	3/9/18 4:41 61	4/9/18 5:46 62	5/9/18 6:51 67	6/9/18 23:56
18 2:36	61	2/9/18 3:41 56	3/9/18 4:46 57	4/9/18 5:51 61	5/9/18 6:56 68	7/9/18 0:01
18 2:41	63	2/9/18 3:46 59 2/9/18 3:51 60	3/9/18 4:51 62 3/9/18 4:56 53	4/9/18 5:56 60 4/9/18 6:01 62	5/9/18 23:01 66 5/9/18 23:06 66	7/9/18 0:06 7/9/18 0:11
18 2:46 18 2:51	65 63	2/9/18 3:51 60 2/9/18 3:56 60	3/9/18 4:56 53 3/9/18 5:01 63	4/9/18 6:01 62 4/9/18 6:06 64	5/9/18 23:06 66 5/9/18 23:11 67	7/9/18 0:11 7/9/18 0:16
18 2:56	62	2/9/18 4:01 59	3/9/18 5:06 61	4/9/18 6:11 64	5/9/18 23:16 66	7/9/18 0:21
18 3:01	62	2/9/18 4:06 59	3/9/18 5:11 63	4/9/18 6:16 64	5/9/18 23:21 67	7/9/18 0:26
18 3:06 18 3:11	66 61	2/9/18 4:11 66 2/9/18 4:16 59	3/9/18 5:16 59 3/9/18 5:21 58	4/9/18 6:21 66 4/9/18 6:26 66	5/9/18 23:26 66 5/9/18 23:31 66	7/9/18 0:31 7/9/18 0:36
18 3:16	62	2/9/18 4:21 55	3/9/18 5:26 59	4/9/18 6:31 66	5/9/18 23:36 66	7/9/18 0:41
18 3:21	60	2/9/18 4:26 64	3/9/18 5:31 61	4/9/18 6:36 67	5/9/18 23:41 65	7/9/18 0:46
18 3:26	60 63	2/9/18 4:31 60 2/9/18 4:36 59	3/9/18 5:36 58	4/9/18 6:41 67	5/9/18 23:46 66	
'18 3:31 '18 3:36	63 61	2/9/18 4:36 59 2/9/18 4:41 60	3/9/18 5:41 62 3/9/18 5:46 62	4/9/18 6:46 67 4/9/18 6:51 68	5/9/18 23:51 67 5/9/18 23:56 65	7/9/18 0:56 7/9/18 1:01
18 3:41	62	2/9/18 4:46 60	3/9/18 5:51 62	4/9/18 6:56 68	6/9/18 0:01 65	7/9/18 1:06
18 3:46	61 50	2/9/18 4:51 60	3/9/18 5:56 63	4/9/18 23:01 66	6/9/18 0:06 66 6/0/18 0:11 66	7/9/18 1:11
'18 3:51 '18 3:56	59 59	2/9/18 4:56 58 2/9/18 5:01 59	3/9/18 6:01 62 3/9/18 6:06 64	4/9/18 23:06 66 4/9/18 23:11 66	6/9/18 0:11 66 6/9/18 0:16 65	7/9/18 1:16 7/9/18 1:21
18 3:56	59 62	2/9/18 5:01 59	3/9/18 6:06 64 3/9/18 6:11 65	4/9/18 23:11 66	6/9/18 0:21 64	7/9/18 1:26
18 4:06	58	2/9/18 5:11 59	3/9/18 6:16 67	4/9/18 23:21 65	6/9/18 0:26 65	7/9/18 1:31
18 4:11	56 50	2/9/18 5:16 64	3/9/18 6:21 69	4/9/18 23:26 65	6/9/18 0:31 65 6/0/18 0:36 64	7/9/18 1:36
/18 4:16 /18 4:21	59 60	2/9/18 5:21 62 2/9/18 5:26 62	3/9/18 6:26 71 3/9/18 6:31 67	4/9/18 23:31 66 4/9/18 23:36 66	6/9/18 0:36 64 6/9/18 0:41 65	7/9/18 1:41 7/9/18 1:46
/18 4:26	62	2/9/18 5:31 59	3/9/18 6:36 67	4/9/18 23:41 65	6/9/18 0:46 64	7/9/18 1:51
/18 4:31	60	2/9/18 5:36 61	3/9/18 6:41 68	4/9/18 23:46 64	6/9/18 0:51 63	7/9/18 1:56
/18 4:36 /18 4:41	61 59	2/9/18 5:41 61 2/9/18 5:46 62	3/9/18 6:46 68 3/9/18 6:51 68	4/9/18 23:51 66 4/9/18 23:56 64	6/9/18 0:56 64 6/9/18 1:01 63	7/9/18 2:01 7/9/18 2:06
	53	2/3/10 3.40 02	0/0/10 0.01 00	4/9/18 23:56 64	0/0/10 1.01 00	1,0/10 2.00

/18 2:11 /18 2:16	57 57	8/9/18 3:16 8/9/18 3:21	62 63	9/9/18 4:21 9/9/18 4:26	57 56	10/9/18 5:26 10/9/18 5:31	63 61	11/9/18 6:31 11/9/18 6:36	66 67	12/9/18 23:36 12/9/18 23:41
/18 2:21	57	8/9/18 3:26	59	9/9/18 4:31	59	10/9/18 5:36	62	11/9/18 6:41	68	12/9/18 23:46
/18 2:26 /18 2:31	45 53	8/9/18 3:31 8/9/18 3:36	61 58	9/9/18 4:36 9/9/18 4:41	60 58	10/9/18 5:41 10/9/18 5:46	63 62	11/9/18 6:46 11/9/18 6:51	67 68	12/9/18 23:51 12/9/18 23:56
/18 2:36	55	8/9/18 3:41	58	9/9/18 4:46	57	10/9/18 5:51	61	11/9/18 6:56	68	13/9/18 0:01
/18 2:41	53	8/9/18 3:46	60	9/9/18 4:51	59	10/9/18 5:56	64	11/9/18 23:01	68	13/9/18 0:06
/18 2:46	51	8/9/18 3:51	60 50	9/9/18 4:56	62	10/9/18 6:01	64	11/9/18 23:06	66 67	13/9/18 0:11
/18 2:51 /18 2:56	45 45	8/9/18 3:56 8/9/18 4:01	59 58	9/9/18 5:01 9/9/18 5:06	55 57	10/9/18 6:06 10/9/18 6:11	64 66	11/9/18 23:11 11/9/18 23:16	67 67	13/9/18 0:16 13/9/18 0:21
/18 3:01	63	8/9/18 4:06	57	9/9/18 5:11	63	10/9/18 6:16	67	11/9/18 23:21	66	13/9/18 0:26
/18 3:06	56	8/9/18 4:11	56	9/9/18 5:16	59	10/9/18 6:21	67	11/9/18 23:26	67	13/9/18 0:31
/18 3:11 /18 3:16	62 58	8/9/18 4:16 8/9/18 4:21	63 61	9/9/18 5:21 9/9/18 5:26	57 58	10/9/18 6:26 10/9/18 6:31	67 67	11/9/18 23:31 11/9/18 23:36	65 67	13/9/18 0:36 13/9/18 0:41
/18 3:21	62	8/9/18 4:26	58	9/9/18 5:31	59	10/9/18 6:36	67	11/9/18 23:41	66	13/9/18 0:46
/18 3:26	45	8/9/18 4:31	62	9/9/18 5:36	60	10/9/18 6:41	68	11/9/18 23:46	65	13/9/18 0:51
/18 3:31 /18 3:36	52 63	8/9/18 4:36 8/9/18 4:41	59 63	9/9/18 5:41 9/9/18 5:46	58 60	10/9/18 6:46 10/9/18 6:51	68 69	11/9/18 23:51 11/9/18 23:56	66 67	13/9/18 0:56 13/9/18 1:01
/18 3:41	52	8/9/18 4:46	60	9/9/18 5:51	61	10/9/18 6:56	70	12/9/18 0:01	65	13/9/18 1:06
/18 3:46	63	8/9/18 4:51	58	9/9/18 5:56	59	10/9/18 23:01	67	12/9/18 0:06	67	13/9/18 1:11
/18 3:51	63	8/9/18 4:56	57	9/9/18 6:01	64	10/9/18 23:06	66	12/9/18 0:11	65	13/9/18 1:16
/18 3:56 /18 4:01	63 58	8/9/18 5:01 8/9/18 5:06	58 61	9/9/18 6:06 9/9/18 6:11	61 63	10/9/18 23:11 10/9/18 23:16	67 67	12/9/18 0:16 12/9/18 0:21	64 72	13/9/18 1:21 13/9/18 1:26
/18 4:06	63	8/9/18 5:11	57	9/9/18 6:16	64	10/9/18 23:21	65	12/9/18 0:26	68	13/9/18 1:31
/18 4:11	62	8/9/18 5:16	60	9/9/18 6:21	68	10/9/18 23:26	65	12/9/18 0:31	69	13/9/18 1:36
/18 4:16 /18 4:21	62 51	8/9/18 5:21 8/9/18 5:26	59 61	9/9/18 6:26 9/9/18 6:31	66 67	10/9/18 23:31 10/9/18 23:36	67 66	12/9/18 0:36 12/9/18 0:41	63 66	13/9/18 1:41 13/9/18 1:46
/18 4:26	62	8/9/18 5:31	61	9/9/18 6:36	66	10/9/18 23:41	65	12/9/18 0:46	67	13/9/18 1:51
18 4:31	63	8/9/18 5:36	60	9/9/18 6:41	66	10/9/18 23:46	65	12/9/18 0:51	63	13/9/18 1:56
'18 4:36 '18 4:41	63 53	8/9/18 5:41	60	9/9/18 6:46 9/9/18 6:51	64 65	10/9/18 23:51	65 65	12/9/18 0:56	63 62	13/9/18 2:01
18 4:41	62	8/9/18 5:46 8/9/18 5:51	60 63	9/9/18 6:56	64	10/9/18 23:56 11/9/18 0:01	65	12/9/18 1:01 12/9/18 1:06	63	13/9/18 2:06 13/9/18 2:11
18 4:51	53	8/9/18 5:56	61	9/9/18 23:01	68	11/9/18 0:06	62	12/9/18 1:11	60	13/9/18 2:16
18 4:56	56	8/9/18 6:01	62	9/9/18 23:06	67	11/9/18 0:11	64	12/9/18 1:16	60	13/9/18 2:21
18 5:01 18 5:06	58 50	8/9/18 6:06 8/9/18 6:11	68 66	9/9/18 23:11 9/9/18 23:16	67 67	11/9/18 0:16 11/9/18 0:21	65 63	12/9/18 1:21 12/9/18 1:26	59 61	13/9/18 2:26 13/9/18 2:31
18 5:06	50 56	8/9/18 6:16	64	9/9/18 23:16	68	11/9/18 0:21	63 65	12/9/18 1:26	62	13/9/18 2:31
18 5:16	58	8/9/18 6:21	66	9/9/18 23:26	68	11/9/18 0:31	63	12/9/18 1:36	58	13/9/18 2:41
18 5:21 18 5:26	60 60	8/9/18 6:26 8/9/18 6:31	66 66	9/9/18 23:31 9/9/18 23:36	67 67	11/9/18 0:36	65 62	12/9/18 1:41	62 57	13/9/18 2:46
18 5:26 18 5:31	60 56	8/9/18 6:31 8/9/18 6:36	66 67	9/9/18 23:36 9/9/18 23:41	67 66	11/9/18 0:41 11/9/18 0:46	62 64	12/9/18 1:46 12/9/18 1:51	57 59	13/9/18 2:51 13/9/18 2:56
18 5:36	61	8/9/18 6:41	66	9/9/18 23:46	70	11/9/18 0:51	62	12/9/18 1:56	54	13/9/18 3:01
18 5:41	61	8/9/18 6:46	67	9/9/18 23:51	66	11/9/18 0:56	62	12/9/18 2:01	56	13/9/18 3:06
18 5:46 18 5:51	61 64	8/9/18 6:51 8/9/18 6:56	67 67	9/9/18 23:56 10/9/18 0:01	67 66	11/9/18 1:01 11/9/18 1:06	61 62	12/9/18 2:06 12/9/18 2:11	57 62	13/9/18 3:11 13/9/18 3:16
18 5:56	59	8/9/18 23:01	67	10/9/18 0:06	66	11/9/18 1:11	63	12/9/18 2:16	60	13/9/18 3:21
18 6:01	63	8/9/18 23:06	67	10/9/18 0:11	64	11/9/18 1:16	59	12/9/18 2:21	59	13/9/18 3:26
18 6:06 18 6:11	65	8/9/18 23:11	67 67	10/9/18 0:16	65	11/9/18 1:21	60	12/9/18 2:26	52	13/9/18 3:31
18 6:16	65 65	8/9/18 23:16 8/9/18 23:21	67 67	10/9/18 0:21 10/9/18 0:26	64 65	11/9/18 1:26 11/9/18 1:31	58 58	12/9/18 2:31 12/9/18 2:36	56 63	13/9/18 3:36 13/9/18 3:41
18 6:21	66	8/9/18 23:26	67	10/9/18 0:31	63	11/9/18 1:36	58	12/9/18 2:41	59	13/9/18 3:46
18 6:26	65	8/9/18 23:31	66	10/9/18 0:36	62	11/9/18 1:41	55	12/9/18 2:46	63	13/9/18 3:51
18 6:31 18 6:36	67 67	8/9/18 23:36 8/9/18 23:41	66 66	10/9/18 0:41 10/9/18 0:46	61 63	11/9/18 1:46 11/9/18 1:51	53 60	12/9/18 2:51 12/9/18 2:56	57 62	13/9/18 3:56 13/9/18 4:01
18 6:41	69	8/9/18 23:46	66	10/9/18 0:51	65	11/9/18 1:56	52	12/9/18 3:01	63	13/9/18 4:06
18 6:46	68	8/9/18 23:51	68	10/9/18 0:56	64	11/9/18 2:01	49	12/9/18 3:06	63	13/9/18 4:11
18 6:51 18 6:56	67 68	8/9/18 23:56 9/9/18 0:01	65 66	10/9/18 1:01 10/9/18 1:06	62 58	11/9/18 2:06 11/9/18 2:11	58 57	12/9/18 3:11 12/9/18 3:16	63 51	13/9/18 4:16 13/9/18 4:21
18 23:01	68	9/9/18 0:06	66	10/9/18 1:11	62	11/9/18 2:16	63	12/9/18 3:21	63	13/9/18 4:26
18 23:06	67	9/9/18 0:11	66	10/9/18 1:16	58	11/9/18 2:21	47	12/9/18 3:26	47	13/9/18 4:31
18 23:11 18 23:16	67 67	9/9/18 0:16	65 65	10/9/18 1:21	59 57	11/9/18 2:26	51 52	12/9/18 3:31	48 63	13/9/18 4:36
18 23:21	67	9/9/18 0:21 9/9/18 0:26	66	10/9/18 1:26 10/9/18 1:31	55	11/9/18 2:31 11/9/18 2:36	52	12/9/18 3:36 12/9/18 3:41	46	13/9/18 4:41 13/9/18 4:46
18 23:26	67	9/9/18 0:31	65	10/9/18 1:36	58	11/9/18 2:41	57	12/9/18 3:46	62	13/9/18 4:51
18 23:31	67	9/9/18 0:36	65	10/9/18 1:41	54	11/9/18 2:46	63	12/9/18 3:51	63	13/9/18 4:56
18 23:36 18 23:41	67 66	9/9/18 0:41 9/9/18 0:46	65 67	10/9/18 1:46 10/9/18 1:51	55 54	11/9/18 2:51 11/9/18 2:56	62 62	12/9/18 3:56 12/9/18 4:01	62 63	13/9/18 5:01 13/9/18 5:06
18 23:46	67	9/9/18 0:51	64	10/9/18 1:56	52	11/9/18 3:01	62	12/9/18 4:06	63	13/9/18 5:11
18 23:51	67	9/9/18 0:56	64	10/9/18 2:01	63	11/9/18 3:06	63	12/9/18 4:11	62	13/9/18 5:16
18 23:56	66	9/9/18 1:01	64	10/9/18 2:06	63	11/9/18 3:11	63 62	12/9/18 4:16	62	13/9/18 5:21 13/9/18 5:26
18 0:01 18 0:06	66 66	9/9/18 1:06 9/9/18 1:11	64 65	10/9/18 2:11 10/9/18 2:16	63 62	11/9/18 3:16 11/9/18 3:21	62	12/9/18 4:21 12/9/18 4:26	63 63	13/9/18 5:31
18 0:11	67	9/9/18 1:16	64	10/9/18 2:21	50	11/9/18 3:26	62	12/9/18 4:31	62	13/9/18 5:36
18 0:16	66	9/9/18 1:21	65	10/9/18 2:26	63	11/9/18 3:31	43	12/9/18 4:36	53	13/9/18 5:41
18 0:21 18 0:26	66 66	9/9/18 1:26 9/9/18 1:31	64 64	10/9/18 2:31 10/9/18 2:36	63 63	11/9/18 3:36 11/9/18 3:41	57 62	12/9/18 4:41 12/9/18 4:46	63 51	13/9/18 5:46 13/9/18 5:51
18 0:31	66	9/9/18 1:36	64 64	10/9/18 2:41	63	11/9/18 3:46	62	12/9/18 4:51	63	13/9/18 5:56
8 0:36	66	9/9/18 1:41	62	10/9/18 2:46	56	11/9/18 3:51	62	12/9/18 4:56	54	13/9/18 6:01
18 0:41 18 0:46	64 65	9/9/18 1:46 9/9/18 1:51	59 61	10/9/18 2:51 10/9/18 2:56	50 62	11/9/18 3:56 11/9/18 4:01	62 62	12/9/18 5:01 12/9/18 5:06	57 58	13/9/18 6:06 13/9/18 6:11
18 0:46	65 65	9/9/18 1:56	61	10/9/18 2:56	62 62	11/9/18 4:01	62 62	12/9/18 5:06	58 52	13/9/18 6:16
18 0:56	65	9/9/18 2:01	59	10/9/18 3:06	62	11/9/18 4:11	60	12/9/18 5:16	54	13/9/18 6:21
8 1:01	64 66	9/9/18 2:06	61 50	10/9/18 3:11	62	11/9/18 4:16	62	12/9/18 5:21	58	13/9/18 6:26
18 1:06 18 1:11	66 64	9/9/18 2:11 9/9/18 2:16	59 61	10/9/18 3:16 10/9/18 3:21	63 56	11/9/18 4:21 11/9/18 4:26	61 62	12/9/18 5:26 12/9/18 5:31	60 58	13/9/18 6:31 13/9/18 6:36
18 1:16	63	9/9/18 2:21	60	10/9/18 3:26	62	11/9/18 4:31	62	12/9/18 5:36	59	13/9/18 6:41
8 1:21	66	9/9/18 2:26	60	10/9/18 3:31	62	11/9/18 4:36	63	12/9/18 5:41	60	13/9/18 6:46
8 1:26 8 1:31	65 62	9/9/18 2:31 9/9/18 2:36	62 62	10/9/18 3:36 10/9/18 3:41	63 55	11/9/18 4:41 11/9/18 4:46	63 62	12/9/18 5:46 12/9/18 5:51	61 63	13/9/18 6:51 13/9/18 6:56
18 1:31	62 62	9/9/18 2:36 9/9/18 2:41	62 61	10/9/18 3:41	55 49	11/9/18 4:46	62 61	12/9/18 5:51	63 62	13/9/18 6:56
18 1:41	63	9/9/18 2:46	61	10/9/18 3:51	62	11/9/18 4:56	54	12/9/18 6:01	64	13/9/18 23:06
18 1:46	62	9/9/18 2:51	64	10/9/18 3:56	61	11/9/18 5:01	63	12/9/18 6:06	64	13/9/18 23:11
18 1:51 18 1:56	64 61	9/9/18 2:56 9/9/18 3:01	61 60	10/9/18 4:01 10/9/18 4:06	47 61	11/9/18 5:06 11/9/18 5:11	55 52	12/9/18 6:11 12/9/18 6:16	65 65	13/9/18 23:16 13/9/18 23:21
18 2:01	62	9/9/18 3:06	60	10/9/18 4:11	45	11/9/18 5:16	63	12/9/18 6:21	68	13/9/18 23:26
18 2:06	62	9/9/18 3:11	62	10/9/18 4:16	63	11/9/18 5:21	55	12/9/18 6:26	67	13/9/18 23:31
18 2:11	62 62	9/9/18 3:16	60 62	10/9/18 4:21	63 55	11/9/18 5:26	59 60	12/9/18 6:31	67 68	13/9/18 23:36
18 2:16 18 2:21	62 63	9/9/18 3:21 9/9/18 3:26	62 63	10/9/18 4:26 10/9/18 4:31	55 62	11/9/18 5:31 11/9/18 5:36	60 59	12/9/18 6:36 12/9/18 6:41	68 69	13/9/18 23:41 13/9/18 23:46
18 2:26	61	9/9/18 3:31	60	10/9/18 4:36	58	11/9/18 5:41	62	12/9/18 6:46	68	13/9/18 23:51
18 2:31	61	9/9/18 3:36	62	10/9/18 4:41	54	11/9/18 5:46	62	12/9/18 6:51	69	13/9/18 23:56
18 2:36	60	9/9/18 3:41	60 50	10/9/18 4:46	62	11/9/18 5:51	60	12/9/18 6:56	69 67	14/9/18 0:01
18 2:41 18 2:46	60 62	9/9/18 3:46 9/9/18 3:51	59 58	10/9/18 4:51 10/9/18 4:56	56 51	11/9/18 5:56 11/9/18 6:01	63 63	12/9/18 23:01 12/9/18 23:06	67 67	14/9/18 0:06 14/9/18 0:11
18 2:51	63	9/9/18 3:56	56	10/9/18 5:01	63	11/9/18 6:06	67	12/9/18 23:11	67	14/9/18 0:16
18 2:56	62	9/9/18 4:01	63	10/9/18 5:06	59	11/9/18 6:11	68	12/9/18 23:16	67	14/9/18 0:21
18 3:01 18 3:06	60 60	9/9/18 4:06	63 55	10/9/18 5:11	60 50	11/9/18 6:16	65 65	12/9/18 23:21	67 66	14/9/18 0:26
	60 61	9/9/18 4:11 9/9/18 4:16	55 59	10/9/18 5:16	50 61	11/9/18 6:21	65 66	12/9/18 23:26 12/9/18 23:31	66 66	14/9/18 0:31 14/9/18 0:36

/9/18 0:41 /9/18 0:46	66 62	15/9/18 1:46 63 15/9/18 1:51 63	16/9/18 2:51 71 16/9/18 2:56 68	17/9/18 3:56 61 17/9/18 4:01 61	18/9/18 5:01 57 18/9/18 5:06 60	19/9/18 6:06 19/9/18 6:11
/9/18 0:51 /9/18 0:56	63 62	15/9/18 1:56 62 15/9/18 2:01 63	16/9/18 3:01 68 16/9/18 3:06 74	17/9/18 4:06 60 17/9/18 4:11 60	18/9/18 5:11 57 18/9/18 5:16 62	19/9/18 6:16 19/9/18 6:21
/9/18 1:01	63	15/9/18 2:06 61	16/9/18 3:11 74	17/9/18 4:16 58	18/9/18 5:21 59	19/9/18 6:26
/9/18 1:06	62	15/9/18 2:11 61	16/9/18 3:16 77	17/9/18 4:21 59	18/9/18 5:26 60	19/9/18 6:31
/9/18 1:11	61	15/9/18 2:16 61	16/9/18 3:21 71	17/9/18 4:26 60	18/9/18 5:31 59	19/9/18 6:36
/9/18 1:16 /9/18 1:21	60 61	15/9/18 2:21 61 15/9/18 2:26 63	16/9/18 3:26 73 16/9/18 3:31 64	17/9/18 4:31 61 17/9/18 4:36 59	18/9/18 5:36 61 18/9/18 5:41 61	19/9/18 6:41 19/9/18 6:46
/9/18 1:26	62	15/9/18 2:31 62	16/9/18 3:36 67	17/9/18 4:41 60	18/9/18 5:46 58	19/9/18 6:51
/9/18 1:31	60	15/9/18 2:36 62	16/9/18 3:41 67	17/9/18 4:46 61	18/9/18 5:51 62	19/9/18 6:56
/9/18 1:36 /9/18 1:41	61 59	15/9/18 2:41 60 15/9/18 2:46 62	16/9/18 3:46 75 16/9/18 3:51 72	17/9/18 4:51 60 17/9/18 4:56 59	18/9/18 5:56 63 18/9/18 6:01 60	19/9/18 23:01 19/9/18 23:06
/9/18 1:46	62	15/9/18 2:51 62	16/9/18 3:56 70	17/9/18 5:01 60	18/9/18 6:06 63	19/9/18 23:11
9/18 1:51	61	15/9/18 2:56 60	16/9/18 4:01 77	17/9/18 5:06 61	18/9/18 6:11 63	19/9/18 23:16
/9/18 1:56 /9/18 2:01	59 58	15/9/18 3:01 62 15/9/18 3:06 60	16/9/18 4:06 73 16/9/18 4:11 70	17/9/18 5:11 60 17/9/18 5:16 62	18/9/18 6:16 65 18/9/18 6:21 66	19/9/18 23:21 19/9/18 23:26
/9/18 2:06	59	15/9/18 3:06 60 15/9/18 3:11 59	16/9/18 4:16 75	17/9/18 5:21 61	18/9/18 6:26 66	19/9/18 23:26 19/9/18 23:31
9/18 2:11	56	15/9/18 3:16 57	16/9/18 4:21 71	17/9/18 5:26 61	18/9/18 6:31 66	19/9/18 23:36
/9/18 2:16	67	15/9/18 3:21 57	16/9/18 4:26 68	17/9/18 5:31 62	18/9/18 6:36 67	19/9/18 23:41
/9/18 2:21 /9/18 2:26	53 50	15/9/18 3:26 63 15/9/18 3:31 58	16/9/18 4:31 71 16/9/18 4:36 68	17/9/18 5:36 61 17/9/18 5:41 62	18/9/18 6:41 67 18/9/18 6:46 68	19/9/18 23:46 19/9/18 23:51
9/18 2:31	52	15/9/18 3:36 60	16/9/18 4:41 63	17/9/18 5:46 62	18/9/18 6:51 67	19/9/18 23:56
9/18 2:36	56	15/9/18 3:41 53	16/9/18 4:46 54	17/9/18 5:51 63	18/9/18 6:56 68	20/9/18 0:01
9/18 2:41 9/18 2:46	63 55	15/9/18 3:46 59 15/9/18 3:51 58	16/9/18 4:51 58 16/9/18 4:56 70	17/9/18 5:56 57 17/9/18 6:01 55	18/9/18 23:01 66 18/9/18 23:06 67	20/9/18 0:06 20/9/18 0:11
9/18 2:51	57	15/9/18 3:56 59	16/9/18 5:01 70	17/9/18 6:06 58	18/9/18 23:11 66	20/9/18 0:16
9/18 2:56	52	15/9/18 4:01 56	16/9/18 5:06 66	17/9/18 6:11 59	18/9/18 23:16 66	20/9/18 0:21
9/18 3:01	55 54	15/9/18 4:06 61 15/9/18 4:11 60	16/9/18 5:11 65 16/9/18 5:16 59	17/9/18 6:16 62 17/9/18 6:21 61	18/9/18 23:21 66 18/9/18 23:26 67	20/9/18 0:26 20/9/18 0:31
9/18 3:06 9/18 3:11	54 58	15/9/18 4:11 60 15/9/18 4:16 57	16/9/18 5:16 59 16/9/18 5:21 64	17/9/18 6:26 62	18/9/18 23:26 67 18/9/18 23:31 66	20/9/18 0:31
9/18 3:16	43	15/9/18 4:21 58	16/9/18 5:26 62	17/9/18 6:31 62	18/9/18 23:36 65	20/9/18 0:41
9/18 3:21	63	15/9/18 4:26 60	16/9/18 5:31 71	17/9/18 6:36 62	18/9/18 23:41 67	20/9/18 0:46
9/18 3:26 9/18 3:31	54 45	15/9/18 4:31 59 15/9/18 4:36 59	16/9/18 5:36 67 16/9/18 5:41 70	17/9/18 6:41 62 17/9/18 6:46 64	18/9/18 23:46 65 18/9/18 23:51 65	20/9/18 0:51 20/9/18 0:56
9/18 3:31	45 49	15/9/18 4:36 59	16/9/18 5:46 75	17/9/18 6:51 63	18/9/18 23:56 66	20/9/18 0:56
9/18 3:41	43	15/9/18 4:46 60	16/9/18 5:51 73	17/9/18 6:56 64	19/9/18 0:01 65	20/9/18 1:06
9/18 3:46 9/18 3:51	58 63	15/9/18 4:51 59 15/9/18 4:56 49	16/9/18 5:56 73 16/9/18 6:01 78	17/9/18 23:01 66 17/9/18 23:06 69	19/9/18 0:06 66 19/9/18 0:11 65	20/9/18 1:11 20/9/18 1:16
9/18 3:51	63	15/9/18 5:01 60	16/9/18 6:06 75	17/9/18 23:00 69	19/9/18 0:16 66	20/9/18 1:16
9/18 4:01	50	15/9/18 5:06 62	16/9/18 6:11 70	17/9/18 23:16 65	19/9/18 0:21 66	20/9/18 1:26
9/18 4:06	62	15/9/18 5:11 59	16/9/18 6:16 73	17/9/18 23:21 66	19/9/18 0:26 64	20/9/18 1:31
9/18 4:11 9/18 4:16	63 63	15/9/18 5:16 59 15/9/18 5:21 62	16/9/18 6:21 74 16/9/18 6:26 76	17/9/18 23:26 64 17/9/18 23:31 65	19/9/18 0:31 66 19/9/18 0:36 65	20/9/18 1:36 20/9/18 1:41
9/18 4:21	56	15/9/18 5:26 59	16/9/18 6:31 76	17/9/18 23:36 63	19/9/18 0:41 65	20/9/18 1:46
/18 4:26	56	15/9/18 5:31 61	16/9/18 6:36 79	17/9/18 23:41 64	19/9/18 0:46 64	20/9/18 1:51
9/18 4:31 9/18 4:36	63 54	15/9/18 5:36 59 15/9/18 5:41 62	16/9/18 6:41 76 16/9/18 6:46 81	17/9/18 23:46 64 17/9/18 23:51 64	19/9/18 0:51 64 19/9/18 0:56 62	20/9/18 1:56 20/9/18 2:01
9/18 4:41	63	15/9/18 5:46 60	16/9/18 6:51 76	17/9/18 23:51 64	19/9/18 0.36 62	20/9/18 2:06
/18 4:46	63	15/9/18 5:51 61	16/9/18 6:56 76	18/9/18 0:01 63	19/9/18 1:06 62	20/9/18 2:11
0/18 4:51	56	15/9/18 5:56 61	16/9/18 23:01 61	18/9/18 0:06 64	19/9/18 1:11 60	20/9/18 2:16
9/18 4:56 9/18 5:01	56 56	15/9/18 6:01 62 15/9/18 6:06 65	16/9/18 23:06 60 16/9/18 23:11 61	18/9/18 0:11 64 18/9/18 0:16 64	19/9/18 1:16 63 19/9/18 1:21 63	20/9/18 2:21 20/9/18 2:26
9/18 5:06	58	15/9/18 6:11 64	16/9/18 23:16 62	18/9/18 0:21 66	19/9/18 1:26 61	20/9/18 2:31
9/18 5:11	58	15/9/18 6:16 64	16/9/18 23:21 60	18/9/18 0:26 67	19/9/18 1:31 61	20/9/18 2:36
9/18 5:16 9/18 5:21	57 58	15/9/18 6:21 68 15/9/18 6:26 68	16/9/18 23:26 62 16/9/18 23:31 62	18/9/18 0:31 61 18/9/18 0:36 62	19/9/18 1:36 58 19/9/18 1:41 60	20/9/18 2:41 20/9/18 2:46
9/18 5:26	62	15/9/18 6:31 67	16/9/18 23:36 61	18/9/18 0:41 62	19/9/18 1:46 56	20/9/18 2:51
9/18 5:31	62	15/9/18 6:36 67	16/9/18 23:41 60	18/9/18 0:46 62	19/9/18 1:51 54	20/9/18 2:56
9/18 5:36 9/18 5:41	59 60	15/9/18 6:41 66 15/9/18 6:46 67	16/9/18 23:46 61 16/9/18 23:51 60	18/9/18 0:51 60 18/9/18 0:56 58	19/9/18 1:56 59 19/9/18 2:01 62	20/9/18 3:01 20/9/18 3:06
9/18 5:46	61	15/9/18 6:51 67	16/9/18 23:56 60	18/9/18 1:01 61	19/9/18 2:06 57	20/9/18 3:11
9/18 5:51	63	15/9/18 6:56 67	17/9/18 0:01 61	18/9/18 1:06 58	19/9/18 2:11 58	20/9/18 3:16
9/18 5:56 9/18 6:01	63 62	15/9/18 23:01 67 15/9/18 23:06 66	17/9/18 0:06 60 17/9/18 0:11 61	18/9/18 1:11 62 18/9/18 1:16 60	19/9/18 2:16 55 19/9/18 2:21 53	20/9/18 3:21 20/9/18 3:26
9/18 6:06	65	15/9/18 23:11 67	17/9/18 0:16 60	18/9/18 1:21 59	19/9/18 2:26 55	20/9/18 3:31
/18 6:11	65	15/9/18 23:16 66	17/9/18 0:21 60	18/9/18 1:26 58	19/9/18 2:31 62	20/9/18 3:36
9/18 6:16	67	15/9/18 23:21 66	17/9/18 0:26 61	18/9/18 1:31 55	19/9/18 2:36 57	20/9/18 3:41
9/18 6:21 9/18 6:26	66 67	15/9/18 23:26 67 15/9/18 23:31 67	17/9/18 0:31 60 17/9/18 0:36 58	18/9/18 1:36 57 18/9/18 1:41 62	19/9/18 2:41 55 19/9/18 2:46 63	20/9/18 3:46 20/9/18 3:51
9/18 6:31	67	15/9/18 23:36 66	17/9/18 0:41 60	18/9/18 1:46 56	19/9/18 2:51 51	20/9/18 3:56
/18 6:36	68	15/9/18 23:41 66	17/9/18 0:46 60	18/9/18 1:51 57	19/9/18 2:56 63	20/9/18 4:01
/18 6:41 /18 6:46	69 68	15/9/18 23:46 66 15/9/18 23:51 64	17/9/18 0:51 60 17/9/18 0:56 60	18/9/18 1:56 57 18/9/18 2:01 63	19/9/18 3:01 63 19/9/18 3:06 63	20/9/18 4:06 20/9/18 4:11
/18 6:51	69	15/9/18 23:56 67	17/9/18 1:01 61	18/9/18 2:06 63	19/9/18 3:11 57	20/9/18 4:16
/18 6:56	69	16/9/18 0:01 66	17/9/18 1:06 57	18/9/18 2:11 57	19/9/18 3:16 61	20/9/18 4:21
/18 23:01 /18 23:06	67 67	16/9/18 0:06 65 16/9/18 0:11 64	17/9/18 1:11 61 17/9/18 1:16 58	18/9/18 2:16 50 18/9/18 2:21 68	19/9/18 3:21 62 19/9/18 3:26 61	20/9/18 4:26 20/9/18 4:31
/18 23:06	67	16/9/18 0:16 68	17/9/18 1:21 60	18/9/18 2:26 63	19/9/18 3:31 62	20/9/18 4:36
/18 23:16	67	16/9/18 0:21 68	17/9/18 1:26 60	18/9/18 2:31 63	19/9/18 3:36 56	20/9/18 4:41
/18 23:21 /18 23:26	68	16/9/18 0:26 69 16/0/18 0:21 69	17/9/18 1:31 59	18/9/18 2:36 52	19/9/18 3:41 56 19/9/18 3:46 61	20/9/18 4:46 20/9/18 4:51
/18 23:26	68 67	16/9/18 0:31 68 16/9/18 0:36 66	17/9/18 1:36 59 17/9/18 1:41 59	18/9/18 2:41 57 18/9/18 2:46 63	19/9/18 3:46 61 19/9/18 3:51 62	20/9/18 4:56
/18 23:36	66	16/9/18 0:41 64	17/9/18 1:46 59	18/9/18 2:51 63	19/9/18 3:56 63	20/9/18 5:01
/18 23:41	66	16/9/18 0:46 61	17/9/18 1:51 60	18/9/18 2:56 40	19/9/18 4:01 58	20/9/18 5:06
/18 23:46 /18 23:51	67 67	16/9/18 0:51 61 16/9/18 0:56 63	17/9/18 1:56 60 17/9/18 2:01 59	18/9/18 3:01 56 18/9/18 3:06 63	19/9/18 4:06 63 19/9/18 4:11 45	20/9/18 5:11 20/9/18 5:16
/18 23:56	66	16/9/18 1:01 65	17/9/18 2:06 59	18/9/18 3:11 54	19/9/18 4:16 63	20/9/18 5:21
/18 0:01	66	16/9/18 1:06 67	17/9/18 2:11 58	18/9/18 3:16 53	19/9/18 4:21 62	20/9/18 5:26
/18 0:06	67	16/9/18 1:11 66	17/9/18 2:16 59	18/9/18 3:21 55	19/9/18 4:26 54	20/9/18 5:31
/18 0:11 /18 0:16	66 67	16/9/18 1:16 67 16/9/18 1:21 63	17/9/18 2:21 58 17/9/18 2:26 58	18/9/18 3:26 49 18/9/18 3:31 54	19/9/18 4:31 57 19/9/18 4:36 62	20/9/18 5:36 20/9/18 5:41
/18 0:21	65	16/9/18 1:26 66	17/9/18 2:31 59	18/9/18 3:36 63	19/9/18 4:41 57	20/9/18 5:46
/18 0:26	65	16/9/18 1:31 67 16/0/18 1:36 64	17/9/18 2:36 60	18/9/18 3:41 54	19/9/18 4:46 62	20/9/18 5:51
/18 0:31 /18 0:36	66 65	16/9/18 1:36 64 16/9/18 1:41 62	17/9/18 2:41 59 17/9/18 2:46 58	18/9/18 3:46 63 18/9/18 3:51 62	19/9/18 4:51 63 19/9/18 4:56 52	20/9/18 5:56 20/9/18 6:01
/18 0:41	65	16/9/18 1:46 64	17/9/18 2:51 59	18/9/18 3:56 61	19/9/18 5:01 53	20/9/18 6:06
9/18 0:46	64	16/9/18 1:51 60	17/9/18 2:56 59	18/9/18 4:01 63	19/9/18 5:06 53	20/9/18 6:11
0/18 0:51	65 65	16/9/18 1:56 63 16/9/18 2:01 65	17/9/18 3:01 60	18/9/18 4:06 62 18/9/18 4:11 56	19/9/18 5:11 59 19/9/18 5:16 57	20/9/18 6:16
9/18 0:56 9/18 1:01	65 64	16/9/18 2:01 65 16/9/18 2:06 70	17/9/18 3:06 58 17/9/18 3:11 58	18/9/18 4:11 56 18/9/18 4:16 58	19/9/18 5:16 57 19/9/18 5:21 59	20/9/18 6:21 20/9/18 6:26
/18 1:06	64	16/9/18 2:11 66	17/9/18 3:16 58	18/9/18 4:21 62	19/9/18 5:26 60	20/9/18 6:31
9/18 1:11	64	16/9/18 2:16 71	17/9/18 3:21 59	18/9/18 4:26 56	19/9/18 5:31 57	20/9/18 6:36
9/18 1:16 9/18 1:21	62 64	16/9/18 2:21 68 16/9/18 2:26 67	17/9/18 3:26 60	18/9/18 4:31 59 18/9/18 4:36 62	19/9/18 5:36 62	20/9/18 6:41
9/18 1:21 9/18 1:26	64 63	16/9/18 2:26 67 16/9/18 2:31 66	17/9/18 3:31 61 17/9/18 3:36 61	18/9/18 4:36 62 18/9/18 4:41 43	19/9/18 5:41 59 19/9/18 5:46 61	20/9/18 6:46 20/9/18 6:51
9/18 1:31	63	16/9/18 2:36 69	17/9/18 3:41 62	18/9/18 4:46 62	19/9/18 5:51 62	20/9/18 6:56
9/18 1:36	64	16/9/18 2:41 67	17/9/18 3:46 56	18/9/18 4:51 62	19/9/18 5:56 62	20/9/18 23:01
9/18 1:41	63	16/9/18 2:46 70	17/9/18 3:51 59	18/9/18 4:56 63	19/9/18 6:01 63	20/9/18 23:06

	Pool time Naise Date	PTN2 (Polloung Kuk Vulloo Mo	Fan Mamarial Sabaal)			
		22/9/18 0:16 66	23/9/18 1:21 63			
	20/9/18 23:26 66	22/9/18 0:31 66	23/9/18 1:36 63	24/9/18 2:41 63	25/9/18 3:46 57	26/9/18 4:51 63
	21/9/18 0:06 65	22/9/18 1:11 65	23/9/18 2:16 62	24/9/18 3:21 62	25/9/18 4:26 62	26/9/18 5:31 56
	21/9/18 0:21 65	22/9/18 1:26 64	23/9/18 2:31 61	24/9/18 3:36 62	25/9/18 4:41 57	26/9/18 5:46 61
	21/9/18 0:46 64	22/9/18 1:51 64	23/9/18 2:56 58	24/9/18 4:01 62	25/9/18 5:06 60	26/9/18 6:11 64
	21/9/18 1:01 62	22/9/18 2:06 62	23/9/18 3:11 62	24/9/18 4:16 62	25/9/18 5:21 58	26/9/18 6:26 66
	21/9/18 1:26 60	22/9/18 2:31 62	23/9/18 3:36 60	24/9/18 4:41 63	25/9/18 5:46 62	26/9/18 6:51 67
Bit No. Bit No. Section 2.55 Control 1.50 Section 2.55	21/9/18 1:41 51	22/9/18 2:46 63	23/9/18 3:51 59	24/9/18 4:56 63	25/9/18 6:01 60	26/9/18 23:06 66
Norma Section						
11 12 16 23 16 12 16 12 16 16 23 16 16 23 16 16 23 16<	21/9/18 1:56 54	22/9/18 3:01 61	23/9/18 4:06 57	24/9/18 5:11 50	25/9/18 6:16 64	26/9/18 23:21 66
1111112216 62 220118 321 60 220118 420 67 240118 620 67 240118 620 67 240118 620 67 240118 620 67 240118 620 67 240118 620 67 240118 620 66 210118 220 63 220118 630 65 220118 641 54 240118 640 61 220118 641 56						
1111 1111 220 220 120 220 120 220 120 220 120 220 120 220 120 220 120 220 120 220 120 220 120 220 120 220 120 220 120 220 120 </td <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>						
111012231 63 229818 3.36 64 229818 4.44 54 24918 5.46 61 25018 6.16 65 24018 2.25 65 111012241 64 62 22918 3.41 51 02918 3.44 55 03 24918 5.61 61 25918 2.51 65 111012241 62 22918 3.51 61 23918 6.51 58 24918 5.61 61 22918 1.25 66 55 24918 5.61 61 22918 1.25 66 55 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 65 24918 5.21 67 25918 5.23 65 24918 5.21 67 25918 5.23 65 24918 5.21 67 25918 5.23 65 24918 5.21 67 <td>21/9/18 2:21 63</td> <td>22/9/18 3:26 57</td> <td>23/9/18 4:31 59</td> <td>24/9/18 5:36 62</td> <td>25/9/18 6:41 64</td> <td>26/9/18 23:46 64</td>	21/9/18 2:21 63	22/9/18 3:26 57	23/9/18 4:31 59	24/9/18 5:36 62	25/9/18 6:41 64	26/9/18 23:46 64
2110 223 51 223 223 83 223 84 55 60 235 65 2110 224 42 220 42 420 42						
21/101 22/16 62 22/101 82/16 61 22/001 82/16 62 22/001 82/16 66 21/011 22/16 63 22/011 83/16 64 22/011 83/16 64 22/011 83/16 64 21/011 23/16 64 22/011 83/16 63 22/011 83/16 65 24/011 86/16 64 22/011 83/16 64 21/011 23/16 64 22/011 83/16 65 24/011 86/16 65 24/011 86/16 65 24/011 86/16 65 24/011 86/16 65 24/011 86/16 65 24/011 86/16 65 24/011 86/16 65 24/011 86/16 65 24/011 86/16 65 24/011 86/16 66 25/011 82/16 66 21/011 83/16 65 22/011 86/16 65 24/011 86/16 67 25/011 82/16 66 24/011 86/16 67 25/011 82/16 66 26/011 86/16 66 24/011 86/16 67 25/011 86/16 66 24/011 86/16 67 25/011 86/16 66 24/011 82/16 67 25/011 86/16 66 <	21/9/18 2:36 51	22/9/18 3:41 55	23/9/18 4:46 58	24/9/18 5:51 60	25/9/18 6:56 66	20/3/10 23.30 03
111012251 63 22018 355 59 23018 550 56 24018 860 63 25018 2318 66 21018 226 22018 4401 56 23018 550 56 24018 821 66 25018 2316 66 21018 350 61 22018 441 56 23018 551 55 24019 821 65 25018 2316 66 21018 3516 53 22018 441 50 23018 552 56 24018 821 67 25018 2336 66 21018 3516 53 22018 4363 56 24018 8461 67 25018 2336 66 21018 3536 63 22018 4363 56 24018 8461 67 25018 2336 66 21018 3546 63 22018 4561 58 24018 8231 67 25018 8336 64 21018 3546 64 22018 8561 56 24018 8336 67 25018 8336 64 21018 356 64 23018 5661 56 24018 2331 67 25018 6361 64 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>						
2101018301 64 2201184305 66 2101018300 61 220118420 60 2201018420 66 2101018300 61 220118420 61 2201018420 65 2101018300 63 220118420 61 220118420 65 2101018300 63 220118420 61 220118420 65 2101018300 63 220118420 64 220118420 65 2101018300 64 2201184420 60 2201184445 60 220118421 64 2101018300 64 2201184430 64 220118444 60 220118464 60 220118464 60 220118464 60 220118464 60 220118464 60 220118464 60 220118464 60 220118464 60 220118464 60 220118464 60 220118464 60 220118464 60 220118666 60 220118666 60 220118666 60 220118666 60 220118666 60 220118666 60 220118666 60 220118666	21/9/18 2:51 63	22/9/18 3:56 59	23/9/18 5:01 58	24/9/18 6:06 63	25/9/18 23:11 66	
21/01/2016 63 220/01/2014/21 61 230/01/52/21 63 240/01/62/31 65 250/01/62/36 65 21/01/63/01 63 220/01/64/36 67 230/01/53/01 63 220/01/63/01 65 21/01/63/01 63 220/01/64/36 67 250/01/63/36 66 21/01/63/01 63 220/01/64/36 60 24/01/66/51 68 220/01/63/36 64 21/01/63/01 63 220/01/64/36 60 24/01/66/51 68 220/01/63/36 64 21/01/63/01 64 220/01/65/51 58 23/01/65/51 62 24/01/66/51 68 25/01/66/21 64 21/01/63/01 64 220/01/65/51 58 23/01/65/51 62 24/01/62/21 67 26/01/60/16 64 21/01/64/01 63 220/01/65/51 58 23/01/65/51 66 24/01/62/21 67 26/01/60/16 64 21/01/64/21 63 220/01/65/51 59 220/01/66/51 61						
21/01/83.16 53 22/01/83.16 53 22/01/83.16 53 25/01/82.38 65 21/01/83.21 63 22/01/83.16 64 22/01/83.16 64 67 25/01/82.38 65 21/01/83.21 63 22/01/83.16 64 66 25/01/82.35 65 21/01/83.21 64 60 23/01/85.46 60 25/01/82.35 64 21/01/83.41 62 22/01/84.46 60 23/01/85.46 62 24/01/85.66 68 25/01/81.06 64 21/01/83.56 64 23/01/85.66 62 24/01/85.67 68 25/01/81.06 64 21/01/85.61 64 23/01/86.61 60 24/01/83.21 67 25/01/80.02 63 21/01/84.06 63 23/01/86.61 61 24/01/83.23 70 25/01/80.02 63 21/01/84.07 63 23/01/86.51 64 23/01/86.51 64 24/01/83.23 70 25/01/80.01 61 21/01/84.21 <td< td=""><td></td><td></td><td></td><td></td><td></td><td></td></td<>						
21/0718326 46 220/0784308 66 220/078207 250/078205 65 21/0718326 63 220/0784308 60 234/078646 67 250/078205 64 21/0718326 63 220/0784308 68 230/07856 68 240/078646 67 250/078205 64 21/0718326 63 220/078606 68 220/078607 61 240/078206 67 250/078006 64 21/0718326 64 220/078607 68 220/078607 61 240/078207 250/078007 64 21/07184367 64 220/078607 65 240/078207 250/078007 250/078007 64 21/07184167 66 220/078627 66 240/078207 250/078007 <td< td=""><td>21/9/18 3:16 53</td><td>22/9/18 4:21 61</td><td>23/9/18 5:26 59</td><td>24/9/18 6:31 65</td><td>25/9/18 23:36 65</td><td></td></td<>	21/9/18 3:16 53	22/9/18 4:21 61	23/9/18 5:26 59	24/9/18 6:31 65	25/9/18 23:36 65	
21/01/14/331 63 22/01/18/341						
214978 83.41 62 229178 43.46 60 233918 65.0 62 249178 65.6 68 269178 0.01 64 214918 83.61 63 229178 65.6 58 239178 65.6 64 239178 65.6 64 214918 84.61 63 229178 65.6 58 239178 65.1 67 269178 0.01 63 214918 44.01 63 229178 55.1 55 239178 65.1 64 249178 23.21 67 269178 0.26 63 214918 44.01 63 229178 53.1 55 239178 65.1 64 249178 23.21 67 269178 0.26 63 214918 44.10 56 229178 53.1 65 239178 63.4 64 249178 23.41 67 269178 0.56 61 214918 44.31 63 229178 53.6 61 239178 64.6 64 249178 23.56 67 269178 0.56 61 214918 44.41 62 229178 55.6 61 239178 0.51 61 259178 0.56 61 259178 0.56 61 214918 45.1 63 229178 55.6 61 239178 0.51 61 25917	21/9/18 3:31 63	22/9/18 4:36 60	23/9/18 5:41 58	24/9/18 6:46 67	25/9/18 23:51 65	
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$						
$ 219/18 3.56 46 \\ 229/18 3.50 45 \\ 229/18 3.51 55 \\ 229/18 5.61 55 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 67 \\ 249/18 2.25 67 \\ 269/18 0.04 61 \\ 219/18 4.31 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 67 \\ 249/18 2.25 67 \\ 269/18 0.04 61 \\ 219/18 4.31 65 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 5.61 67 \\ 249/18 2.25 67 \\ 269/18 0.04 61 \\ 219/18 4.41 62 \\ 229/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 6.51 65 \\ 249/18 2.25 67 \\ 269/18 0.16 61 \\ 219/19 4 4.6 \\ 54 \\ 239/18 5.61 65 \\ 239/18 5.61 65 \\ 239/18 6.51 65 \\ 249/18 2.51 67 \\ 269/18 0.16 61 \\ 219/19 4 5.6 63 \\ 229/18 5.61 65 \\ 239/18 5.20 67 \\ 269/18 0.16 61 \\ 219/18 4.51 65 \\ 229/18 5.61 65 \\ 239/18 5.21 67 \\ 269/18 0.16 61 \\ 219/18 4.51 65 \\ 229/18 5.61 65 \\ 239/18 2.51 67 \\ 269/18 0.16 67 \\ 269/18 1.16 62 \\ 219/18 4.51 65 \\ 239/18 2.51 67 \\ 269/18 1.16 61 \\ 219/18 4.51 65 \\ 239/18 2.51 66 \\ 259/18 0.16 67 \\ 269/18 1.16 61 \\ 219/18 4.51 65 \\ 239/18 2.51 65 \\ 259/18 0.21 66 \\ 269/18 0.16 67 \\ 269/18 1.15 55 \\ 219/18 5.11 64 \\ 239/18 2.31 66 \\ 259/18 0.26 65 \\ 269/18 0.11 66 \\ 269/18 1.15 55 \\ 219/18 5.1 65 \\ 239/18 2.31 66 \\ 299/18 2.31 66 \\ 299/18 2.31 66 \\ 299/18 2.31 66 \\ 299/18 2.31 66 \\ 299/18 2.31 65 \\ 299/18 2$						
219/18 4-06 63 229/18 5-11 55 239/18 6-16 61 249/18 2-26 67 289/18 0-31 62 219/18 4-16 65 229/18 5-21 62 239/18 6-26 65 249/18 2-36 61 289/18 0-36 61 219/18 4-31 63 229/18 5-36 69 239/18 6-36 64 249/18 2-36 67 289/18 0-36 61 219/18 4-31 63 229/18 5-36 61 239/18 6-36 67 289/18 0-56 61 219/18 4-31 63 229/18 5-46 63 239/18 6-61 65 249/18 2-51 67 289/18 0-56 61 219/18 4-51 64 229/18 5-56 64 239/18 8-51 65 259/18 0-11 67 289/18 1-16 60 289/18 1-16 66 289/18 1-16 67 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66 289/18 1-16 66<	21/9/18 3:56 46	22/9/18 5:01 58	23/9/18 6:06 58	24/9/18 23:11 67	26/9/18 0:16 64	
219/918.4:11 65 229/918.5:16 58 239/918.6:21 66 249/918.2:33 68 269/918.0:36 61 219/918.4:21 63 229/918.5:26 61 239/918.6:31 64 249/918.2:33 68 269/918.0:36 61 219/918.4:21 63 229/918.5:35 59 239/918.6:36 64 249/918.2:35 67 259/918.0:36 61 219/918.4:36 63 229/918.5:41 63 239/918.6:36 65 249/918.2:55 67 289/918.0:56 61 219/918.4:46 50 229/918.5:51 64 239/918.6:56 65 249/918.2:56 67 289/918.1:16 62 219/918.4:56 63 229/918.5:56 61 239/918.2:36 65 259/918.0:16 67 269/918.1:16 62 259/918.1:16 62 259/918.1:16 62 259/918.1:16 62 259/918.0:16 66 259/918.0:16 67 269/918.1:16 62 259/918.0:16 63 259/918.0:16 66 259/918.0:16 65 259/918.0:16 65 259/918.0:16 67 269/918.1:16 65 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>						
219/18.4/21 63 229/18.5/6 61 239/18.6/31 66 249/18.2/36 70 280/18.0/46 61 219/18.4/31 63 229/18.5/36 61 239/18.6/36 66 249/18.2/316 67 280/18.0/51 61 219/18.4/31 63 229/18.5/36 64 239/18.6/3 65 249/18.2/36 67 280/18.0/56 61 219/18.4/1 62 229/18.5/3 64 239/18.6/5 65 249/18.2/36 67 280/18.1/1 61 219/18.4/1 62 229/18.6/5 64 239/18.6/5 65 250/18.0/1 67 280/18.1/1 61 219/18.5/6 63 229/18.6/1 64 239/18.2/1 67 250/18.0/1 67 280/18.1/1 61 219/18.5/6 63 229/18.6/1 64 239/18.2/1 67 250/18.0/1 67 280/18.1/1 61 250/18.0/1 67 280/18.1/3 55 260/18.1/3 55 260/18.1/3 55 260/18.1/3 55 260/18.1/3 55 260/18.1/3 55 260/18.1/3 55	21/9/18 4:11 63	22/9/18 5:16 58	23/9/18 6:21 66	24/9/18 23:26 67	26/9/18 0:31 62	
219/18.4:31 63 229/18.5:36 61 239/18.6:41 64 24/9/18.23:51 67 269/18.0:56 61 219/18.4:41 62 229/18.5:46 63 239/18.6:51 65 24/9/18.23:51 67 269/18.10.0 61 219/19.4:41 62 229/18.5:56 64 239/18.6:56 65 24/9/18.23:56 67 269/18.10.0 61 219/18.4:56 63 229/18.5:56 64 239/18.6:51 65 24/9/18.23:56 67 269/18.11 62 219/18.5:16 63 229/18.6:51 64 239/18.23:16 66 259/18.0:16 67 269/18.13 55 219/18.5:16 63 229/18.6:31 64 239/18.23:36 64 259/18.0:36 66 269/18.13 65 219/18.5:26 59 229/18.6:31 64 239/18.23:36 64 259/18.0:36 66 269/18.13 65 219/18.5:36 59 229/18.6:31 67 239/18.23:4 64 259/18.0:36 65 269/18.14 62 219/18.5:36 59 229/18.6:31						
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$						
219/18 4.46 50 229/18 5.5 6.4 239/18 6.5 259/18 0.01 67 269/18 1.16 6.2 219/18 4.56 63 229/18 6.01 67 259/18 0.11 67 269/18 1.16 62 219/18 5.06 64 239/18 239/18 6.6 259/18 0.21 67 269/18 1.26 59 219/18 5.6 58 229/18 6.6 259/18 0.21 67 269/18 1.36 60 219/18 51 64 239/18 23.1 66 259/18 0.31 66 269/18 1.36 60 219/18 5.5 229/18 6.6 239/18 23.11 64 259/18 0.41 72 269/18 1.46 55 219/18 5.6 67 239/18 23.11 64 259/18 0.41 72 269/18 1.46 55 219/18 5.6 67 239/18 23.11 65 259/18 0.51	21/9/18 4:36 58	22/9/18 5:41 63	23/9/18 6:46 64	24/9/18 23:51 67	26/9/18 0:56 61	
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 4:51 54	22/9/18 5:56 61	23/9/18 23:01 66	25/9/18 0:06 67	26/9/18 1:11 62	
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$						
21/9/18 6:16 63 22/9/18 6:21 64 23/9/18 2:32 65 25/9/18 0:36 66 26/9/18 1:31 60 21/9/18 5:26 59 22/9/18 6:36 73 23/9/18 2:33 64 25/9/18 0:46 72 26/9/18 1:51 55 21/9/18 5:36 59 22/9/18 6:66 73 23/9/18 2:34 65 25/9/18 0:46 68 26/9/18 1:56 58 21/9/18 5:41 60 22/9/18 6:66 73 23/9/18 2:356 64 25/9/18 0:56 52 26/9/18 2:01 63 21/9/18 5:51 63 22/9/18 6:56 67 24/9/18 0:01 64 25/9/18 1:06 65 26/9/18 2:11 62 21/9/18 5:56 59 22/9/18 2:316 67 24/9/18 0:01 63 25/9/18 1:11 65 26/9/18 2:21 55 21/9/18 6:16 64 22/9/18 2:316 67 24/9/18 0:21 63 25/9/18 1:16 65 26/9/18 2:36 47 21/9/18 6:16 66 22/9/18 2:326 67 24/9/18 0:21 63 25/9/18 1:31 64 26/9/18 2:36 47 21/9/18 6:16	21/9/18 5:06 58	22/9/18 6:11 64	23/9/18 23:16 66	25/9/18 0:21 67	26/9/18 1:26 59	
$ \begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 5:16 63	22/9/18 6:21 64	23/9/18 23:26 65	25/9/18 0:31 66	26/9/18 1:36 60	
21/9/18 5:31 59 22/9/18 6:41 66 23/9/18 23:41 64 25/9/18 0:46 72 26/9/18 1:51 65 21/9/18 5:64 60 22/9/18 6:46 68 23/9/18 23:51 64 25/9/18 0:56 65 26/9/18 1:21 63 21/9/18 5:64 63 22/9/18 6:56 67 24/9/18 0:01 64 25/9/18 1:06 65 26/9/18 2:16 63 21/9/18 5:65 59 22/9/18 23:06 67 24/9/18 0:01 64 25/9/18 1:16 65 26/9/18 2:21 56 21/9/18 5:06 64 22/9/18 23:16 67 24/9/18 0:16 63 25/9/18 1:16 65 26/9/18 2:21 56 21/9/18 6:16 64 22/9/18 23:16 67 24/9/18 0:16 63 25/9/18 1:31 64 26/9/18 2:36 47 21/9/18 6:16 66 22/9/18 23:26 67 24/9/18 0:36 63 25/9/18 1:31 64 26/9/18 2:36 63 21/9/18 6:16 66 22/9/18 23:36 67 24/9/18 0:36 63 25/9/18 1:36 64 26/9/18 2:36 62 21/9/18 6:36 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 5:31 59	22/9/18 6:36 73	23/9/18 23:41 64	25/9/18 0:46 72	26/9/18 1:51 55	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$				25/9/18 1:01 66	26/9/18 2:06 54	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 5:56 59	22/9/18 23:01 67	24/9/18 0:06 65	25/9/18 1:11 65	26/9/18 2:16 63	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 6:11 63	22/9/18 23:16 67	24/9/18 0:21 63	25/9/18 1:26 64	26/9/18 2:31 62	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 6:26 67	22/9/18 23:31 67	24/9/18 0:36 63	25/9/18 1:41 64	26/9/18 2:46 63	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 6:51 68	22/9/18 23:56 69	24/9/18 1:01 62	25/9/18 2:06 64	26/9/18 3:11 62	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 23:06 67	23/9/18 0:11 65	24/9/18 1:16 59	25/9/18 2:21 64	26/9/18 3:26 63	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	21/9/18 23:16 67	23/9/18 0:21 65	24/9/18 1:26 60	25/9/18 2:31 70	26/9/18 3:36 63	
21/9/18 23:31 67 23/9/18 0:36 65 24/9/18 1:41 51 25/9/18 2:46 64 26/9/18 3:51 62 21/9/18 23:36 67 23/9/18 0:41 65 24/9/18 1:46 63 25/9/18 2:51 66 26/9/18 3:56 61 21/9/18 23:46 67 23/9/18 0:46 64 24/9/18 1:51 58 25/9/18 2:56 62 26/9/18 4:01 62 21/9/18 23:46 67 23/9/18 0:51 64 24/9/18 1:56 51 25/9/18 3:01 63 26/9/18 4:06 63 21/9/18 23:51 66 23/9/18 0:56 65 24/9/18 1:56 51 25/9/18 3:06 64 26/9/18 4:06 63 21/9/18 23:56 67 23/9/18 0:56 65 24/9/18 1:206 62 25/9/18 3:06 64 26/9/18 4:11 62 21/9/18 23:56 67 23/9/18 1:01 64 24/9/18 2:06 62 25/9/18 3:16 64 26/9/18 4:16 62 22/9/18 0:01 66 23/9/18 1:06 64 24/9/18 2:16 63 25/9/18 3:11 64 26/9/18 4:16 62 22/9/18 0:01 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>						
21/9/18 23:41 66 23/9/18 0:46 64 24/9/18 1:51 58 25/9/18 2:56 62 26/9/18 4:01 62 21/9/18 23:46 67 23/9/18 0:51 64 24/9/18 1:56 51 25/9/18 3:01 63 26/9/18 4:06 63 21/9/18 23:51 66 23/9/18 0:56 65 24/9/18 2:01 62 25/9/18 3:01 64 26/9/18 4:11 62 21/9/18 23:56 67 23/9/18 1:01 64 24/9/18 2:01 62 25/9/18 3:06 64 26/9/18 4:11 62 22/9/18 0:01 66 23/9/18 1:06 64 24/9/18 2:16 62 25/9/18 3:11 64 26/9/18 4:21 50 22/9/18 0:01 66 23/9/18 1:06 64 24/9/18 2:16 56 25/9/18 3:12 60 26/9/18 4:21 50 22/9/18 0:06 66 23/9/18 1:11 65 24/9/18 2:16 56 25/9/18 3:21 60 26/9/18 4:26 63	21/9/18 23:31 67	23/9/18 0:36 65	24/9/18 1:41 51	25/9/18 2:46 64	26/9/18 3:51 62	
21/9/18 23:46 67 23/9/18 0:51 64 24/9/18 1:56 51 25/9/18 3:01 63 26/9/18 4:06 63 21/9/18 23:51 66 23/9/18 0:56 65 24/9/18 2:01 62 25/9/18 3:06 64 26/9/18 4:11 62 21/9/18 23:56 67 23/9/18 1:01 64 24/9/18 2:06 62 25/9/18 3:11 64 26/9/18 4:11 62 22/9/18 0:01 66 23/9/18 1:06 64 24/9/18 2:16 63 25/9/18 3:12 60 26/9/18 4:21 50 22/9/18 0:06 66 23/9/18 1:11 65 24/9/18 2:16 56 25/9/18 3:21 60 26/9/18 4:26 63						
21/9/18 23:56 67 23/9/18 1:01 64 24/9/18 2:06 62 25/9/18 3:11 64 26/9/18 4:16 62 22/9/18 0:01 66 23/9/18 1:06 64 24/9/18 2:11 63 25/9/18 3:16 61 26/9/18 4:21 50 22/9/18 0:06 66 23/9/18 1:11 65 24/9/18 2:16 56 25/9/18 3:21 60 26/9/18 4:26 63	21/9/18 23:46 67	23/9/18 0:51 64	24/9/18 1:56 51	25/9/18 3:01 63	26/9/18 4:06 63	
22/9/18 0:06 66 23/9/18 1:11 65 24/9/18 2:16 56 25/9/18 3:21 60 26/9/18 4:26 63	21/9/18 23:56 67	23/9/18 1:01 64	24/9/18 2:06 62	25/9/18 3:11 64	26/9/18 4:16 62	
	22/9/18 0:11 66	23/9/18 1:16 62	24/9/18 2:21 45	25/9/18 3:26 61	26/9/18 4:31 61	I

	Real-time Noise Data			11/9/18 13:31 66	17/9/18 8:01 61	21/9/18 14:31 65
		31/8/18 13:01 63	6/9/18 7:31 62		17/9/18 8:31 62	21/9/18 15:01 65
Serie Las Serie Las <t< td=""><td></td><td></td><td></td><td></td><td></td><td></td></t<>						
	27/8/18 11:31 65	31/8/18 18:01 61	6/9/18 12:31 63	12/9/18 7:01 59	17/9/18 13:31 63	22/9/18 8:01 63
	27/8/18 13:01 67	1/9/18 7:31 61	6/9/18 14:01 66	12/9/18 8:31 63	17/9/18 15:01 65	22/9/18 9:31 66
	27/8/18 14:31 67	1/9/18 9:01 68	6/9/18 15:31 65	12/9/18 10:01 63	17/9/18 16:31 63	22/9/18 11:01 64
	27/8/18 16:01 67	1/9/18 10:31 66	6/9/18 17:01 66		17/9/18 18:01 61	22/9/18 12:31 61
27240 4.00 6 100 16 3.01 6 70 16 7.01 6 100 16 8.01 6 220 18 5.01 10 280 4.00 100 16 1.01 6 70 16 7.01 6 120 16 1.01 6 120 16 1.01 6 220 18 5.01 7 7	27/8/18 17:31 67			12/9/18 13:01 68		22/9/18 14:01 63
Setter 201 66 198/18 201 66 198/18 201 66 198/18 201 67 298/18 201 63 298/18 201 64 298/18 201 65 298/18 201 65 298/18 201 65 298/18 201 65 198/18 201 67 298/18 201 65 298/18 201 65 198/18 201 67 298/18 201 65 298/18 201 65 198/18 201 67 298/18 201 65 298/18 201 65 298/18 201 65 298/18 201 65 298/18 201 65 298/18 201 66 198/18 201 66 298/18 201 66 198/18 201 66 298/18 201 66 198/18 201 66 298/18 201 66 198/18 201 66 298/18 201 66 198/18 201 66 298/18 201 66 198/18 201 66 298/18 201 66 298/18 201 66 298/18 201 66 298/18 201 66 298/18 201 66 298/18 201 66 298/18 201 66 298/18 201 66 298/18						
State Bit of the second seco						
abster abster<						
Bits Part Constraint Constraint <thconstraint< th=""> Constraint <thconstraint< th=""> Constraint Constraint</thconstraint<></thconstraint<>						
Base in thom 66 198/16 16:31 66 270/16 11:31 68 120/16 17:31 62 198/16 12:31 63 220/16 17:31 62 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 63 220/16 17:31 64 180/16 16:31 66 220/16 17:31 64 180/16 16:31 66 220/16 17:31 64 180/16 16:31 64 220/16 17:31 64 220/16 17:31 64 220/16 17:31 66 220/16 17:31 66 220/16 17:31 67 220/16 17:31 64 220/16 17:31 66 220/16 17:31 66 220/16 17:31 66 220/16 17:31 66 220/16 17:31 66 220/16 17:31 66 220/16 17:31 66 220/16 17:31 66 220/16 17:31						
abserts bits 198/16 1/20 city 776/16 1/201 city 776/16 1/201 city 120/16 1/201 city 24/04 77.01 60 255/11 1/201 65 198/16 1/201 65 198/16 1/201 65 198/16 1/201 65 24/04 77.01 62 24/04 77.01 62 24/04 77.01 62 24/04 77.01 62 24/04 77.01 62 24/04 77.01 62 24/04 77.01 62 24/04 77.01 62 24/04 77.01 62 24/04 77.01 63 24/04 80.01 64 24/04 80.01 66						
BESIENT 111 66 19918 1621 66 13918 1771 60 19918 1621 66 13918	28/8/18 10:31 66	1/9/18 17:01 64	7/9/18 11:31 66	12/9/18 18:01 61	18/9/18 12:31 62	24/9/18 7:01 60
Bits Field 65 19978 field 66 13978 7731 62 19978 field 65 24048 531 66 28808 16331 67 3978 503 64 19978 1631 64						
Baster 1330 68 39818 72.31 63 7.9418 14.01 67 13918 80.1 64 15918 15.01 68 2424 80.1 68 Baster 1330 64 39818 16.31 64 39818 16.31 64 39818 16.31 64 24418 15.01 66 24418 15.01 67 24418 15.01 67 24418 15.01 67 24418 15.01 67 24418 15.01 67 <	28/8/18 12:01 65	1/9/18 18:31 65	7/9/18 13:01 66	13/9/18 7:31 62	18/9/18 14:01 65	24/9/18 8:31 68
Bases Constraint Constraint </td <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>						
Balanti 1531 66 39818 1531 66 7.918 15.31 66 7.918 15.31 67 7.918 15.31 67 7.918 15.31 67 7.918 15.31 66 2.4491 15.31 67 2.4491 15.31 66 2.4491 15.31 66 2.4491 15.31 67 2.4491 15.31 66 2.4491 15.31 67 2.4491 15.31 66 2.4491 15.31 67 2.4491 15.31 66 2.4491 15.31 66 2.4491 15.31	28/8/18 13:31 67	3/9/18 8:01 64	7/9/18 14:31 67	13/9/18 9:01 64	18/9/18 15:31 68	24/9/18 10:01 66
Base 16 501 64 398 18 531 66 244 18 1331 67 139 18 13 77 139 18 13 771 63 244 18 13 71 66 280 18 1531 62 39 78 11 701 63 244 18 13 71 66 139 18 13 71 66 139 18 13 71 66 139 18 12 71 66 139 18 12 71 66 139 18 12 71 66 139 18 12 71 66 139 18 12 71 66 139 18 12 71 66 139 18 12 71 66 139 18 12 71 68 244 18 13 71 68 244 18 13 71 68 244 18 13 71 68 139 18 12 71 68 139 18 12 71 68 139 18 12 71 68 244 18 13 71 68 244 18 13 71 68 244 18 13 71 68 139 18 14 16 71 68 244 18 13 71 68 244 18 13 71 68 244 18 13 71 68 244 18 13 71 68 244 18 13 71 68 244 18 13 71 68 244 18 13 71 67 244 18 13 71 67 244 18 13 71 67 244 18 13 71 67 244 18 13 71 67 244 18 13 71						
Baber Composition Composition <thcomposition< th=""> <thc< td=""><td></td><td></td><td></td><td></td><td></td><td></td></thc<></thcomposition<>						
abeline Constraint						
Base 17:31 62 30/18 12:01 67 70/18 18:31 66 130/18 13:01 66 140/18 5:01 62 24/18 18:01 62 200/18 16:01 62 30/18 12:31 66 100/18 12:31 66 100/18 12:31 66 100/18 12:31 66 100/18 12:31 66 100/18 12:31 66 100/18 12:31 66 100/18 12:31 66 100/18 12:31 67 100/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 67 120/18 12:31 68 120/18 12:31 68 120/18 12:31 68 120/18 12:31 68 120/18 12:31 68 120/18 12:31 68 120/18 12:31 68 120/18 12:31 68 120/18 12:31 68 120/18 12:3						
288/19 100/18 63 39/19 12.31 66 109/18 661 62 24/08 11.51 66 288/19 100/18						
288/16 60 398/16 731 64 1398/16 1401 67 199/16 631 62 249/18 1501 66 298/16 631 631 631 631 64 1399/18 1501 66 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 1399/18 1501 64 249/18 1601 66 249/18 1601 65 249/18 1601 65 249/18 1601 65 249/18 1601 65 249/18 1601 65 249/18 1601 65 249/18 1601 65 249/18 1601 65 249/18 1601 65 249/18 1601						
200/17/31 62 30/17/11-01 66 130/17/81-01 65 190/17/81-00 67 240/07/81-601 67 200/17/81-01 65 30/181-00 65 30/181-00 67 240/07/81-00 67 240/07/81-00 67 240/07/81-00 67 240/07/81-00 67 240/07/81-00 67 240/07/81-00 67 240/07/81-00 67 240/07/81-00 67 240/07/81-00 66 240/07/81-00 67 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 67 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 66 240/07/81-00 67 240/07/81-00 67 240/07/81-00 66 240/07/81-00 66 240/07/81-00<	28/8/18 18:31 60	3/9/18 13:01 65	8/9/18 7:31 64	13/9/18 14:01 67	19/9/18 8:31 62	24/9/18 15:01 68
Besine 801 62 39/16 801 63 19/16 801 64 39/16 801 64 39/16 801 64 39/16 801 65 24/97 8 801 66 24/97 8 813 66 24/97 8 801 66 24/97 8 801 66 24/97 8 801 66 24/97 8 801 66 24/97 8 801 66 24/97 8 801 66 24/97 8 801 66 24/97 8 801 66 24/97 8 801 66 24/97 8 801						
gamma bit 65 39/11 501 67 B9/16 1001 66 139/18 101 67 249/18 113 65 39/18 1101 66 139/18 1101 67 249/18 1131 66 249/18 1131 <	29/8/18 8:01 62	3/9/18 14:31 66	8/9/18 9:01 68	13/9/18 15:31 65	19/9/18 10:01 67	24/9/18 16:31 67
28/07/8931 65 39/07/81631 66 89/07/81731 64 199/07/81731 66 24/07/81831 66 28/07/81031 65 39/07/81631 66 28/07/81301 64 199/07/81231 66 28/07/81301 66 28/07/81201 66 39/07/81301 64 199/07/81301 66 28/07/81301						
28/3/110:31 65 39/18 17:31 64 89/18 12:31 65 199/18 12:31 65 28/17 17:31 62 28/3/11:131 68 39/18 17:31 64 89/18 12:31 64 199/18 13:31 65 28/17 15:31 62 28/17 15:31 62 28/17 15:31 66 28/17 15:31 62 28/17 15:31 66 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 66 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 28/17 15:31 62 18/17 16 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65 18/17 16:31 65	29/8/18 9:31 65	3/9/18 16:01 66	8/9/18 10:31 66	13/9/18 17:01 65	19/9/18 11:31 66	24/9/18 18:01 66
Barkin 11:01 66 39/16 12:01 64 139/16 18:01 65 199/16 18:00 65 26/0718 18:01 66 29/0718 11:20 66 39/16 18:01 66 29/0718 18:01 66 29/0718 18:01 66 29/0718 18:01 66 29/0718 18:01 64 199/16 18:01 66 29/0718 18:01 64 199/171 18:01 65 199/1718 18:01 66 29/0718 18:01 64 29/0718 18:01 64 199/171 16:01 66 29/0718 18:01 64 29/0718 18:01 64 29/0718 18:01 65 149/078 9:01 64 199/171 16:01 64 29/0718 18:01 65 149/078 9:01 64 199/171 16:01 64 29/0718 18:01 65 149/078 9:01 64 199/171 16:01 64 29/0718 18:01 65 149/078 10:01 64 29/0718 10:01 67 29/0718 18:01 65 149/078 10:01 64 29/0718 7:01 65 29/0718 7:01 65 29/0718 7:01 65 29/0718 7:01 65 29/0718 7:01 65 29/0718 10:01 <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td></th<>						
Barkin 12:01 66 39/16 13:01 66 14/0718 7:31 64 199718 14:01 66 25/0718 2:31 63 29/0718 12:31 62 49/16 7:31 64 39/16 13:01 65 14/0718 2:01 64 199718 14:31 66 25/0718 2:01 65 199718 14:31 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 65 26/0718 2:01 66 26/0718 1:03 66 26/0718 1:03 66 26/0718 1:03 66 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 64 26/0718 2:01 66 26/0718						
28/8/18 1231 64 49/18 701 63 89/18 1331 66 14/9/18 231 61 19/9/18 14/31 65 28/9/18 1531 66 28/9/18 1331 62 49/9/18 231 65 14/9/18 231 61 19/9/18 1531 65 28/9/18 14/31 65 14/9/18 931 65 19/9/18 1631 63 28/9/18 14/31 65 14/9/18 931 65 19/9/18 1631 63 28/9/18 1631 63 28/9/18 1631 63 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 64 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631 66 28/9/18 1631						
298/18 1331 62 44/918 64 99/18 14/918 65 14/918 63 199/18 1531 65 14/918 199/18 1531 65 14/918 199/18 1531 65 14/918 199/18 1531 65 14/918 199/18 1531 65 14/918 199/18 1531 65 14/918 199/18 1531 63 26/918 11.01 62 26/918 11.01 62 26/918 11.01 62 26/918 11.01 62 26/918 11.01 64 26/918 11.01 64 26/918 11.01 64 26/918 11.01 64 26/918 11.01 65 14/918 10.918 13.918 10.918						
298/18 14/01 62 4/9/18 209/18 15.01 65 199/18 16.01 64 209/18 13.01 62 298/18 13.01 66 4/9/18 10.01 65 199/18 16.01 63 226/18 11.01 62 226/18 11.01 63 126/18 <td></td> <td></td> <td></td> <td></td> <td></td> <td></td>						
298/18 14/31 60 4/9/18 90/18 16:31 65 199/18 16:31 63 226/18 15:31 68 226/18 15:31 68 49/18 13:31 66 39/18 16:31 63 14/9/18 11:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 199/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66 209/18 16:31 66						
298/08 16 149/08 11/01 66 199/08 12/01 22/08/08 60 199/08 12/01 62 28/07/08 63 149/08 11/01 66 199/08 12/01 62 28/07/08 12/01 63 28/07/08 12/01 64 199/08 13/01 65 28/07/08 13/01 66 29/07/08 13/01 65 28/07/08 13/01 66 29/07/08 13/01 65 28/07/08 13/01 66 29/07/08 13/01 65 28/07/08 13/01 66 29/07/08 13/01 65 28/07/08 13/01 66 14/01/08 13/01 67 28/07/08 13/01 66 29/01/08 13/01 67 28/07/08 14/01/08 13/01 66 28/01/08 13/01 67 28/01/08 13/01 66 28/01/08 13/01 67 28/01/08 13/01 66 28/01/08 13/01 66 28/01/08 13/01 66 28/01/08 13/0	29/8/18 14:31 60		8/9/18 15:31 65	14/9/18 10:01 65	19/9/18 16:31 63	
29/07/8 16:01 66 8/9/8 17:01 63 14/9/18 13:31 66 19/9/18 16:01 61 28/9/18 16:01 67 29/9/18 17:01 68 49/18 11:31 64 29/9/18 10:01 65 29/9/18 10:01 65 26/9/18 10:01 65 26/9/18 10:01 65 26/9/18 10:01 65 26/9/18 10:01 65 26/9/18 10:01 65 26/9/18 10:01 65 26/9/18 10:01 65 26/9/18 10:01 66 20/9/18 61 62 20/9/18 61 62 26/9/18 14:01 65 20/9/18 61 62 20/9/18 61 62 20/9/18 10:01 68 14/9/18 10:01 66 20/9/18 10:01 68 14/9/18 10:01 66 20/9/18 10:01 68 14/9/18 10:01 68 14/9/18 10:01 68 26/9/18 10:01						
29/8/18 1/2/18	29/8/18 16:01 68	4/9/18 10:31 66	8/9/18 17:01 63	14/9/18 11:31 66	19/9/18 18:01 61	26/9/18 12:31 66
298/18 137.31 66 499/18 12.01 63 89/18 13.31 66 209/18 209/18 66 209/18 14.31 65 298/18 18.31 68 49/18 13.31 67 109/18 7.31 66 209/18 23.31 63 28/97.18 15.31 64 308/18 7.31 66 49/18 15.31 64 209/18 53.3 63 14/97.81 50.0 66 209/18 53.3 68 28/97.18 16.3 16.4 308/18 63 14/97.81 66 14/97.81 66 209/18 10.31 67 28/97.18 16.2 209/18 10.31 66 209/18 10.31 66 209/18 10.31 66 209/18 13.31 68 28/97.18 16.2 209/18 13.31 66 209/18 13.31 66 209/18 13.31 66 209/18 13.31 66 209/18 13.31 66						
28/8/18 16/8 4/9/18 10/9/18 61 14/9/18 14/9/18 63 26/9/18 63 26/9/18 63 26/9/18 63 26/9/18 63 26/9/18 63 26/9/18 63 26/9/18 63 26/9/18 64 26/9/18 64 26/9/18 64 26/9/18 64 26/9/18 64 26/9/18 64 26/9/18 64 26/9/18 64 26/9/18 64 26/9/18 64 26/9/18 65 26/9/18 65 26/9/18 65 26/9/18 16.2 <	29/8/18 17:31 68	4/9/18 12:01 63	8/9/18 18:31 65	14/9/18 13:01 66	20/9/18 7:31 66	26/9/18 14:01 65
308/18 7:01 66 49/8 13:31 48 109/18 8:01 61 149/18 14:31 67 209/18 9:01 67 269/18 15:31 64 308/18 731 66 49/18 14:01 67 109/18 8:01 65 209/18 15:31 64 308/18 8:01 65 49/18 15:31 66 109/18 9:01 66 149/18 15:01 65 209/18 10:01 68 269/18 10:31 62 308/18 9:01 64 49/18 15:31 65 109/18 10:01 66 149/18 16:01 65 209/18 11:01 68 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 62 269/18 11:31 63 209/18 11:31 63 209/18 11:31 63 209/18 11:31 63 209/18 11:31 64 269/18 11:31						
30/8/18.01 65 49/8 14:31 66 10/9/18.901 66 14/9/18 15:31 65 20/9/18 10:01 68 26/9/18 16:31 62 30/8/18.831 64 49/9/18 15:31 65 10/9/18 10:01 66 14/9/18 16:31 65 20/9/18 11:01 68 26/9/18 11:01 68 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 26/9/18 11:01 66 20/9/18 11:01 66 20/9/18 11:01 66 20/9/18 11:01 66 20/9/18 11:01 66 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01 67 20/9/18 11:01	30/8/18 7:01 66	4/9/18 13:31 48	10/9/18 8:01 61	14/9/18 14:31 67	20/9/18 9:01 67	26/9/18 15:31 64
30/8/18 64 49/9/8 15.01 66 14/9/8 16.01 66 20/9/18 10.01 67 26/9/18 17.01 62 30/8/18 65 49/9/18 16.51 65 10/9/18 10.31 66 14/9/18 17.01 65 20/9/18 11.31 66 26/9/18 13.1 66 26/9/18 13.1 66 26/9/18 13.1 66 26/9/18 13.1 66 26/9/18 13.1 66 20/9/18 13.1 66 26/9/18 13.1 66 20/9/18 13.1 66 20/9/18 13.1 66 20/9/18 13.1 66 20/9/18 13.1 66 20/9/18 13.1 66 20/9/18 13.1 66 20/9/18 13.1 66 20/9/18 14.9 10.9 13.1 66 20/9/18 14.9 10.9 13.1 66 20/9/18 14.9 11.9 13.1 67 20/9/18 13.1 67 20/9/18 13.1						
30/8/18 9:31 65 4/9/18 10/9/18 10:31 66 14/9/18 17:31 63 20/9/18 11:31 66 26/9/18 18:31 62 30/8/18 10:31 66 4/9/18 17:31 63 20/9/18 12:31 66 20/9/18 12:31 64 14/9/18 13:31 66 Normal Day 19:00-23:00. 30/8/18 11:31 66 4/9/18 12:31 64 15/9/18 13:31 68 Normal Day 19:00-23:00. 30/8/18 11:31 66 4/9/18 13:31 65 15/9/18 13:31 65 20/9/18 14:31 67 30/8/18 13:31 65 5/9/18 13:31 65 15/9/18 16:31 63 20/9/18 15:31 68 27/8/18 19:01 62 30/8/18 13:31 65 5/9/18 10:31 65 15/9/18 10:01 66 20/9/18 16:31 67 27/8/18 19:11 62	30/8/18 8:31 64	4/9/18 15:01 66	10/9/18 9:31 66	14/9/18 16:01 66	20/9/18 10:31 67	26/9/18 17:01 62
30/8/18 10:01 66 4/9/18 17:01 65 10/9/18 11:01 66 14/9/18 17:31 63 20/9/18 12:01 66 22/9/18 12:31 66 30/8/18 10:01 66 4/9/18 17:31 63 10/9/18 11:31 64 14/9/18 18:31 61 20/9/18 12:31 66 Normal Day 19:00-23:00. 30/8/18 11:21 64 14/9/18 18:31 61 20/9/18 13:31 68 Normal Day 19:00-23:00. 30/8/18 12:21 65 5/9/18 7:01 60 10/9/18 13:31 65 15/9/18 7:31 63 20/9/18 14:31 67 27/8/18 19:01 62 30/8/18 12:31 65 5/9/18 7:01 60 10/9/18 14:31 65 15/9/18 8:01 64 20/9/18 15:01 67 27/8/18 19:01 62 30/8/18 14:31 65 5/9/18 8:01 62 10/9/18 15:31 65 15/9/18 9:01 66 20/9/18 15:31 68 27/8/18 19:16 64 30/8/18 14:31 65 5/9/18 9:31 65 10/9/18 15:31 65 15/9/18 10:01 66 20/9						
30/8/18 11:01 66 4/9/18 13:01 63 10/9/18 12:01 64 14/9/18 18:01 63 20/9/18 13:01 68 Normal Day 19:00-23:00. 30/8/18 12:01 65 4/9/18 18:31 63 10/9/18 12:31 64 15/9/18 7:31 63 20/9/18 13:31 68 20/9/18 13:31 68 20/9/18 13:31 63 20/9/18 13:31 63 20/9/18 13:31 63 20/9/18 13:31 65 5/9/18 0:01 62 20/9/18 13:31 63 20/9/18 15:31 68 27/8/18 19:01 62 30/8/18 13:31 65 5/9/18 0:01 62 10/9/18 15:01 65 15/9/18 0:01 63 20/9/18 15:31 68 27/8/18 19:01 62 30/8/18 14:31 65 5/9/18 0:01 63 10/9/18 15:01 65 15/9/18 0:01 66 20/9/18 16:31 67 27/8/18 19:16 64 30/8/18 15:31 64 5/9/18 0:01 63 10/9/18 16:31 65 15/9/18 10:31 66 20/9/18 17:31 65 27/8/18 19:21 63 30/8/18 15:31	30/8/18 10:01 66	4/9/18 16:31 66	10/9/18 11:01 66	14/9/18 17:31 63	20/9/18 12:01 66	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						Normal Day 19:00.22:00
30/8/18 12:01 65 4/9/18 13:01 63 10/9/18 13:01 65 15/9/18 7:31 63 20/9/18 14:31 67 07:00-23:00 30/8/18 12:31 65 5/9/18 7:31 61 10/9/18 14:31 65 20/9/18 15:01 67 27/8/18 19:01 62 30/8/18 13:31 65 5/9/18 63 10/9/18 14:31 65 15/9/18 9:01 62 27/8/18 19:06 63 30/8/18 14:31 65 5/9/18 9:01 62 10/9/18 15:31 65 15/9/18 10:01 66 20/9/18 16:31 67 27/8/18 19:16 64 30/8/18 15:31 64 5/9/18 9:31 63 10/9/18 16:31 63 15/9/18 11:31 66 20/9/18 18:31 65 27/8/18 19:31 62 30/8/18 17:01 64 5/9/18 10:0	30/8/18 11:31 66	4/9/18 18:01 62	10/9/18 12:31 64	15/9/18 7:01 63	20/9/18 13:31 68	Sunday & Holiday
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	30/8/18 12:01 65	4/9/18 18:31 63	10/9/18 13:01 65	15/9/18 7:31 63	20/9/18 14:01 67	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$						27/8/18 19:01 62
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	30/8/18 13:31 65	5/9/18 8:01 62	10/9/18 14:31 65	15/9/18 9:01 66	20/9/18 15:31 68	27/8/18 19:06 63
30/8/18 15:01 64 5/9/18 9:31 63 10/9/18 16:01 65 15/9/18 10:31 66 20/9/18 17:01 67 27/8/18 19:21 63 30/8/18 16:01 64 5/9/18 10:01 63 10/9/18 16:31 63 15/9/18 11:01 67 20/9/18 17:01 65 27/8/18 19:26 63 30/8/18 16:01 64 5/9/18 10:01 63 10/9/18 17:01 63 15/9/18 11:01 65 20/9/18 17:31 65 27/8/18 19:36 62 30/8/18 16:31 65 5/9/18 11:31 65 10/9/18 18:01 63 15/9/18 12:31 62 20/9/18 17:31 64 27/8/18 19:46 62 30/8/18 17:31 64 5/9/18 12:31 65 11/9/18 7:31 61 15/9/18 13:31 62 21/9/18 7:31 65 27/8/18 19:46 62 30/8/18 18:01 66 5/9/18 13:01 66 11/9/18 7:31 61 15/9/18 13:31 62 21/9/18 8:01 65 27/8/18 19:46 62 30/8/18 18:01 64 5/9/18 13:31 66<						
30/8/18 16:01 64 5/9/18 10:31 64 10/9/18 17:01 63 15/9/18 11:31 66 20/9/18 18:01 65 27/8/18 19:31 62 30/8/18 16:31 65 5/9/18 11:31 65 10/9/18 17:31 63 15/9/18 12:01 63 20/9/18 18:31 65 27/8/18 19:36 62 30/8/18 16:31 64 5/9/18 12:01 64 10/9/18 18:31 60 15/9/18 13:01 64 21/9/18 7:31 65 27/8/18 19:41 61 30/8/18 18:01 66 5/9/18 12:31 65 11/9/18 7:31 64 21/9/18 7:31 65 27/8/18 19:41 61 30/8/18 18:01 66 11/9/18 7:01 60 15/9/18 13:31 62 21/9/18 8:31 65 27/8/18 19:56 61 31/8/18 7:01 64 5/9/18 13:31 66 11/9/18 8:31 67 21/9/18 8:31 68 27/8/18 20:01 60 31/8/18 7:31 64 15/9/18 16:31 67 21/9/18 9:31 68 27/8/18 20:01 60 31/8/18 8:01	30/8/18 15:01 64	5/9/18 9:31 63	10/9/18 16:01 65	15/9/18 10:31 66	20/9/18 17:01 67	27/8/18 19:21 63
30/8/18 16:31 65 5/9/18 11:01 67 10/9/18 17:31 63 15/9/18 12:01 63 20/9/18 18:31 65 27/8/18 19:36 62 30/8/18 17:31 64 5/9/18 11:31 65 10/9/18 18:01 63 15/9/18 12:31 62 21/9/18 7:31 64 27/8/18 19:46 62 30/8/18 17:31 64 5/9/18 12:01 64 10/9/18 18:01 60 15/9/18 13:31 62 21/9/18 7:31 65 27/8/18 19:46 62 30/8/18 18:01 66 5/9/18 13:01 66 11/9/18 7:31 61 15/9/18 13:31 62 21/9/18 8:01 66 27/8/18 19:56 61 31/8/18 7:01 64 5/9/18 13:31 66 11/9/18 8:01 62 15/9/18 14:01 67 21/9/18 9:01 68 27/8/18 20:01 60 31/8/18 7:31 64 5/9/18 14:31 65 11/9/18 9:01 67 15/9/18 15:31 67 21/9/18 9:01 68 27/8/18 20:11 61 31/8/18 8:01 64 5/9/18 15:01 65						
30/8/18 17:31 64 5/9/18 12:01 64 10/9/18 18:31 60 15/9/18 13:01 64 21/9/18 7:31 65 27/8/18 19:46 62 30/8/18 18:01 66 5/9/18 12:31 65 11/9/18 7:31 61 15/9/18 13:31 62 21/9/18 8:31 66 27/8/18 19:56 61 30/8/18 18:01 64 5/9/18 13:31 66 11/9/18 7:31 61 15/9/18 13:31 67 21/9/18 8:01 68 27/8/18 19:56 61 31/8/18 7:31 64 11/9/18 8:31 66 11/9/18 8:31 64 15/9/18 15:01 67 21/9/18 9:01 68 27/8/18 20:01 60 31/8/18 8:01 64 5/9/18 15:01 65 11/9/18 9:01 67 21/9/18 10:01 68 27/8/18 20:01 60 31/8/18 8:01 64 5/9/18 15:01 65 11/9/18 9:01 67 15/9/18 16:01 67 21/9/18 10:01 68 27/8/18 20:01 60 31/8/18 8:01 65 5/9/18 16:01 64 11/9/18 10:01 67	30/8/18 16:31 65	5/9/18 11:01 67	10/9/18 17:31 63	15/9/18 12:01 63	20/9/18 18:31 65	27/8/18 19:36 62
30/8/18 18:01 66 5/9/18 12:31 65 11/9/18 7:01 60 15/9/18 13:31 62 21/9/18 8:01 66 27/8/18 19:51 62 30/8/18 18:31 65 5/9/18 13:01 66 11/9/18 7:31 61 15/9/18 13:31 67 21/9/18 8:01 68 27/8/18 19:56 61 31/8/18 7:01 64 5/9/18 13:31 66 11/9/18 8:01 62 15/9/18 14:31 67 21/9/18 9:01 68 27/8/18 20:06 60 31/8/18 7:31 64 5/9/18 14:01 66 11/9/18 8:01 67 21/9/18 9:01 68 27/8/18 20:06 60 31/8/18 8:01 64 5/9/18 14:01 65 11/9/18 9:01 67 21/9/18 10:01 68 27/8/18 20:16 60 31/8/18 8:01 67 5/9/18 15:01 65 11/9/18 9:01 67 15/9/18 16:01 67 21/9/18 10:01 68 27/8/18 20:16 60 31/8/18 9:01 67 5/9/18 16:01 64 11/9/18 10:01 67 15/9/18 11:01 67						
31/8/18 7:01 64 5/9/18 13:31 66 11/9/18 8:01 62 15/9/18 14:31 67 21/9/18 9:01 68 27/8/18 20:01 60 31/8/18 7:31 64 5/9/18 14:01 66 11/9/18 8:31 64 15/9/18 15:01 67 21/9/18 9:01 68 27/8/18 20:01 60 31/8/18 8:01 64 5/9/18 14:31 65 11/9/18 8:31 64 15/9/18 15:01 67 21/9/18 10:01 68 27/8/18 20:01 60 31/8/18 8:31 66 5/9/18 15:01 65 11/9/18 9:31 68 15/9/18 16:01 67 21/9/18 10:31 67 21/9/18 10:31 67 27/8/18 20:16 60 31/8/18 9:01 65 5/9/18 15:01 65 11/9/18 10:01 67 15/9/18 16:31 62 21/9/18 11:01 67 27/8/18 20:16 60 31/8/18 9:01 65 5/9/18 16:01 64 11/9/18 10:01 67 15/9/18 16:31 62 21/9/18 11:01 67 27/8/18 20:26 59 31/8/18 10:01 65	30/8/18 18:01 66	5/9/18 12:31 65	11/9/18 7:01 60	15/9/18 13:31 62	21/9/18 8:01 66	27/8/18 19:51 62
31/8/18 7:31 64 5/9/18 14:01 66 11/9/18 8:31 64 15/9/18 15:01 67 21/9/18 9:31 68 27/8/18 20:06 60 31/8/18 8:31 64 5/9/18 14:31 65 11/9/18 9:01 67 15/9/18 15:31 67 21/9/18 10:01 68 27/8/18 20:16 60 31/8/18 8:31 66 5/9/18 15:01 65 11/9/18 9:01 67 15/9/18 16:31 67 21/9/18 10:01 68 27/8/18 20:16 60 31/8/18 9:01 67 5/9/18 15:01 65 11/9/18 10:01 67 21/9/18 11:01 67 21/9/18 10:01 68 27/8/18 20:21 60 31/8/18 9:01 65 5/9/18 16:01 64 11/9/18 10:01 67 15/9/18 17:01 62 21/9/18 11:31 67 27/8/18 20:21 60 31/8/18 10:01 65 5/9/18 16:01 64 11/9/18 11:01 67 15/9/18 17:01 62 21/9/18 11:31 67 27/8/18 20:24 60 31/8/18 10:01 65 5/9/18 16:31 63						
31/8/18 8:01 64 5/9/18 14:31 65 11/9/18 9:01 67 15/9/18 15:31 67 21/9/18 10:01 68 27/8/18 20:11 61 31/8/18 8:01 66 5/9/18 15:01 65 11/9/18 9:31 68 15/9/18 16:01 67 21/9/18 10:01 67 21/9/18 10:01 67 27/8/18 20:16 60 31/8/18 9:01 67 5/9/18 16:01 64 11/9/18 10:01 67 15/9/18 16:31 62 21/9/18 11:01 67 27/8/18 20:26 59 31/8/18 9:01 65 5/9/18 16:01 64 11/9/18 10:01 67 15/9/18 17:01 62 21/9/18 11:01 67 27/8/18 20:26 59 31/8/18 10:01 65 5/9/18 16:01 63 11/9/18 11:01 67 15/9/18 17:01 62 21/9/18 11:01 67 27/8/18 20:31 62 31/8/18 10:01 65 5/9/18 17:01 63 11/9/18 11:01 65 15/9/18 18:01 62 21/9/18 12:01 62 21/9/18 12:01 65 27/8/18 20:46 63		5/9/18 14:01 66	11/9/18 8:31 64	15/9/18 15:01 67	21/9/18 9:31 68	27/8/18 20:06 60
31/8/18 9:01 67 5/9/18 15:31 65 11/9/18 10:01 67 15/9/18 16:31 62 21/9/18 11:01 67 27/8/18 20:21 60 31/8/18 9:01 65 5/9/18 16:01 64 11/9/18 10:31 68 15/9/18 17:01 62 21/9/18 11:31 67 27/8/18 20:26 59 31/8/18 10:01 65 5/9/18 16:31 63 11/9/18 11:01 67 15/9/18 17:01 62 21/9/18 11:31 67 27/8/18 20:26 59 31/8/18 10:01 65 5/9/18 16:31 63 11/9/18 11:01 67 15/9/18 17:31 63 21/9/18 12:01 64 27/8/18 20:26 63 31/8/18 11:01 65 5/9/18 17:01 63 11/9/18 12:01 62 21/9/18 12:01 67 27/8/18 20:46 63 31/8/18 11:01 65 5/9/18 17:01 63 11/9/18 12:01 62 21/9/18 13:01 67 27/8/18 20:46 60 31/8/18 11:31 65 5/9/18 18:01 63 11/9/18 12:31 61 17/9/18 7:01 5			11/9/18 9:01 67			
31/8/18 9:31 65 5/9/18 16:01 64 11/9/18 10:31 68 15/9/18 17:01 62 21/9/18 11:31 67 27/8/18 20:26 59 31/8/18 10:01 65 5/9/18 16:31 63 11/9/18 11:01 67 15/9/18 17:31 63 21/9/18 11:201 64 27/8/18 20:26 59 31/8/18 10:01 65 5/9/18 16:31 63 11/9/18 11:01 67 15/9/18 17:31 63 21/9/18 12:01 64 27/8/18 20:31 62 31/8/18 11:01 65 5/9/18 17:01 63 11/9/18 12:01 62 21/9/18 12:31 65 27/8/18 20:36 63 31/8/18 11:01 65 5/9/18 17:31 63 11/9/18 12:01 62 21/9/18 13:31 65 27/8/18 20:46 63 31/8/18 11:31 65 5/9/18 18:01 63 11/9/18 12:31 61 17/9/18 7:01 59 21/9/18 13:31 65 27/8/18 20:46 60	31/8/18 9:01 67			15/9/18 16:31 62	21/9/18 11:01 67	27/8/18 20:21 60
31/8/18 10:31 66 5/9/18 17:01 63 11/9/18 11:31 65 15/9/18 18:01 62 21/9/18 12:31 65 27/8/18 20:36 63 31/8/18 11:01 65 5/9/18 17:31 63 11/9/18 12:01 62 15/9/18 18:31 62 21/9/18 13:01 67 27/8/18 20:41 63 31/8/18 11:31 65 5/9/18 18:01 63 11/9/18 12:31 61 17/9/18 7:01 59 21/9/18 13:31 65 27/8/18 20:46 60	31/8/18 9:31 65		11/9/18 10:31 68	15/9/18 17:01 62	21/9/18 11:31 67	27/8/18 20:26 59
31/8/18 11:01 65 5/9/18 17:31 63 11/9/18 12:01 62 15/9/18 18:31 62 21/9/18 13:01 67 27/8/18 20:41 63 31/8/18 11:31 65 5/9/18 18:01 63 11/9/18 12:31 61 17/9/18 7:01 59 21/9/18 13:31 65 27/8/18 20:46 60						
	31/8/18 11:01 65	5/9/18 17:31 63	11/9/18 12:01 62	15/9/18 18:31 62	21/9/18 13:01 67	27/8/18 20:41 63

	22:21 60 22:26 61 22:31 60
277014 2121 0.3 20014 2226 0.4 19018 0.2 2918 2.24 0.4 2918 2.24 2.24 2.24 2.24 2.24 2.24 2.	
2779 18 6 300/18 10/18 20/18 12/26 6/2 20/18 22/26 20/18 <td></td>	
	19:36 62
2771 2236 64 300/15 100/15 201/15 201/15 201/15 201/12	
27/14 22.36 62 305/14 19.41 60 19.18 20.16 13.55 80 20.18 13.55 80 20.18 13.55 80 20.18 13.55 80 20.18 13.55 80 20.18 13.55 80 20.18 13.55 80 20.18 13.55 80 20.18 13.55 80 20.18 13.55 80 20.18 13.55	19:51 62
27701 22.41 63 300611 19.46 61 10.71 22.56 63 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 75 30.71 12.56 30.71 <	
27719122251 62 309119106 60 13918201 51 291191406 56 53119111 64 53418 27719122251 62 309119201 60 13918211 64 53418 5311911 64 53418 53418 54119150 65 53418 54119150 65 309119120 65 53418 54119151 65 309119120 65 53418 54119151 65 309119120 65 53911911 65	20:06 62
272/14/12/256 63 308/14 20:01 69 10/16 21:06 55 20/16 14:11 64 30/16 10:16 63 50/16 3 288/16 10:11 60 308/16 20:01 66 10/16 21:11 66 20/16 14:26 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:31 65 30/16 10:36 65 30/16 10:36 65 30/16 10:36 65 30/16 10:36 65 30/16 10:36 65 50/16 20/16 11:45 67 30/16 10:36 66 50/16 30/16 10:36 50/16 57 30/16 10:36 66 50/16 50 30/16 10:36 50/16 50 30/16 10:36 50/16 50 30/16 20:16 65 50/16 50 30/16 20:16 65 50/16 30/16 20:16 65 50/16 50	
288/1810-06 60 30/1618/20.11 60 10/16/21.16 66 20/1614/21 63 30/1618/20.16 63 50/16/20.16 288/1810-11 60 30/1618/20.16 58 10/16/21.16 57 20/1614/20 67 30/1618/20.16 59 50/16/20.26 57 30/1618/20.16 59 50/16/20.26 57 30/1618/20.16 59 50/16/20.26 57 30/1618/20.16 59 10/16/21.46 57 30/1618/20.16 59 10/16/21.46 57 30/1618/20.16 59 10/16/21.46 57 30/1618/20.16 50 10/16/22.16 57 30/1618/20.16 50 10/16/22.26 57 20/1618/20.16 50 30/1618/20.16 50 10/16/22.21 57 20/1618/20.16 50 30/1618/20.16 50 30/16/20.16 50 30/1618/20.16 50 30/1618/20.16 50 30/16/20.16 50 30/16/20.16 50 30/16/20.16 50 30/16/20.16 50 30/16/20.16 50 30/16/20.16 50 30/16/20.16 50<	20:21 64
288/11 1011 2011 2011 1011 2011 <	
280/16/19/21 56 300/16/19/228 58 19/16/21/36 57 29/16/14/36 57 39/16/19/36 63 59/16/2 220/16/16/26 42 300/16/20/16 50 10/16/21/36 57 39/16/16/36 59/16/2 220/16/16/26 53 300/16/20/26 61 10/16/21/36 59 39/16/16/26 57 39/16/16/26 59/16/2 220/16/16/26 54 300/16/20/26 56 10/16/21/26 59/16/2 30/16/16/20/26 59/16/2 220/16/16/26 54 300/16/20/16 50 30/16/16/20/26 59 30/16/20/26 59/16/2 59	20:36 63
288/18 19:13 57 30:01:8:20:36 59 19:118:21:41 56 29:19:8:14:46 57 39:11:8:10:16 66 59:19:8: 288/18 19:33 30:01:8:20:46 60 19:11:8:21:5 57 29:19:8:14:41 56 39:11:8:20:16 65 39:11:8:20:16 65 39:11:8:20:16 65 39:11:8:20:16 65 39:11:8:20:16 63 59:19:8:20:8 59:19:8:20:8 59:19:8:20:8 59:19:8:20:8 59:19:8:20:8 59:19:8:20:8 59:19:8:20:8:20:8 59:19:8:20:8:20:8:20:8:20:8:20:8:20:8:20:8:2	
28/0718 19/06 53 30/0718 20/0718 14/51 50 30/0718 20/0718 28/0718 19/04 55 30/0718 20/0718 10/0718	
288/078 1956 60 1/9/18 22:01 57 29/18 15:06 57 39/18 20:11 62 59/18 20:11 288/078 1956 60 30/078 21:05 58 20/18 15:16 59 39/18 20:16 63 59/18 20:15 288/078 20:16 58 30/078 21:16 59 30/078 20:16 59 39/18 20:16 63 59/178 288/078 20:16 58 30/078 21:16 59 19/078 22:15 57 29/078 15:36 59 39/18 20:36 64 59/078 288/078 20:26 56 29/078 15:36 62 39/078 20:36 65 59/078 288/078 20:36 64 19/18 22:35 57 29/078 15:36 62 39/078 20:36 65 59/078 288/078 20:46 69 30/078 21:46 60 1/0718 22:57 62 29/078 15:36 62 39/078 21:05 59 59/078 288/078 20:46 69 30/078 21:46 63 29/078 17:06 29/078 17:06 59 39/078 21:07 59 39/078 21:07 59<	
288/18 2006 68 308/18 21:11 60 19/18 22:15 58 29/18 15:21 59 39/18 20:21 63 59/18 288/18 20:11 63 308/18 21:11 60 19/18 22:25 54 29/18 15:21 59 39/18 20:26 65 59/18 288/18 20:16 63 308/18 21:16 60 19/18 22:25 57 29/18 15:31 59 39/18 20:26 65 59/18 288/18 20:16 63 308/18 21:1 53 19/18 22:45 56 29/18 15:46 60 39/18 20:56 58 59/18 <td>21:16 61</td>	21:16 61
288/078 200/07 58 200/07 59 30/07/12/22/8 63 59/07 288/078 200/07 58 30/07/12/22/8 57 20/07 59 30/07/12/22/8 57 20/07 59 30/07/12/22/8 57 20/07 59 30/07/12/22/8 57 20/07 59 30/07/12/22/8 57 20/07 59 30/07/12/22/8 57 20/07 50 30/07/12/22/8 57 20/07 50 30/07/12/22/8 50 30/07/12/22/8 50 30/07 50/07 50/07/12/22/8 50 30/07/12/22/8 50 30/07/12/22/8 50/07/12/8 <	
280/18 20:16 56 30/18 21:21 59 10/18 22:26 57 20/18 15:36 62 30/18 20:26 55 30/18 20:26 59 30/18 20:26 59 30/18 20:26 59 30/18 20:26 59 30/18 20:26 50 50/18 20 50/18 20 50/18 20 50/18 20 50/18 20 50/18 20 50/18 20 50/18 20 5	21:31 63
$ \begin{array}{c c c c c c c c c c c c c c c c c c c $	21:46 61
28/8/18 20:36 61 30/8/18 21:41 59 10/8/18 22:46 56 29/8/18 50:51 59 30/8/18 20:46 56 59/176 28/8/18 20:46 59 30/8/18 21:41 52 10/9/8 22:56 44 29/8/18 10:16 50 30/8/18 21:61 59 59/176 28/8/18 20:56 58 30/8/18 21:61 63 29/8/18 20:66 30/8/18 21:16 61 50/8/18 28/8/18 20:16 58 30/8/18 21:16 63 29/8/18 10:16 58 30/8/18 21:16 61 50/8/18 28/8/18 21:11 56 30/8/18 22:16 63 29/9/18 72:16 63 29/9/18 16:31 58 30/8/18 21:36 57 59/9/18 28/8/18 21:24 57 30/8/18 22:36 64 29/9/18 7:31 64 29/9/18 16:31 58 30/8/18 21:46 62 59/9/18 28/8/18 21:45 56 30/8/18 22:46 63 29/9/18 16:41 59 39/9/18 21:46 62 59/9/18 28/8/18 21:45 56 30/8/18 22:46 63 29/9/	
228/018 20:46 59 300/018 21:51 52 11/018 22:56 44 20/018 16:06 59 30/018 21:16 59 50/018 21:11 59 50/018 21:11 59 50/018 21:11 59 50/018 21:11 59 50/018 21:11 59 30/018 21:16 50 50/018 50/018 50/018 50/018 50/018 50 50/018 50 50/018 50/018 50/018 50/018	22:01 61
288/18 20:56 69 30/8/18 22:01 63 29/18 16:11 69 30/8/18 21:16 61 59/18 288/18 21:06 66 30/8/18 22:16 63 29/18 7:16 63 29/18 16:16 59 30/8/18 21:26 58 55/8/18 288/18 21:16 66 30/8/18 22:21 61 29/18 7:16 63 29/18 16:31 56 30/8/18 21:36 57 55/8/18 288/18 21:16 66 30/8/18 22:21 61 29/18 7:26 63 29/18 16:31 53 30/9/18 21:36 57 56/8/18 28/8/18 21:26 57 30/8/18 22:31 46 29/18 7:36 63 29/18 16:41 56 30/9/18 21:46 62 50/176 28/8/18 21:31 53 30/8/18 22:41 46 29/18 7:41 63 29/18 16:51 57 30/9/18 22:46 63 29/18 17:06 57 30/9/18 22:41 62 60/178 28/8/18 21:51 55 30/8/18 22:56 37 29/18 8:01 60 29/18 17:06 57 30/9/18 22:26 <td></td>	
288/18 21:01 68 30/01/8 22:06 62 29/01/87:11 65 29/01/81 61:16 69 30/01/82 21:16 65 288/18 21:11 65 30/01/8 22:16 63 29/01/87 21 63 29/01/81 62:26 62 30/01/8 22:36 57 55/01/85 28/01/81 21:11 65 30/01/8 22:26 64 29/01/87 7:31 64 29/01/81 63:6 63 30/01/8 22:26 64 29/01/87 7:31 64 29/01/81 63:6 63 30/01/8 22:46 62 55/01/85 28/01/81 21:41 63 30/01/8 22:46 45 29/01/87 7:46 63 29/01/81 64:46 56 30/01/8 22:46 62 69/01/81 28/01/82 1:41 62 30/01/8 22:46 45 29/01/87 7:46 63 29/01/81 7:56 57 30/01/8 22:16 62 69/01/81 28/01/82 1:41 63 30/01/8 22:46 45 29/01/87 7:56 53 30/01/8 22:16 62 69/01/81 28/01/82 1:16 53 30/01/8 22:16 7 29/01/8 17:06 57	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	
288/18 21/16 56 30/18 22.21 51 20/18 72.65 50/18 23/18 16.13 56 30/18 13.36 57 50/18 288/18 12.16 57 30/8/18 22.31 46 20/18 7.31 64 20/18 7.31 64 20/18 7.36 63 20/18 16.46 56 30/18 12.46 55 50/18 2 28/18 12.11 52 30/18 12.56 57 30/18 12.56 62 60/11 30/18 12.66 59 30/18 22.01 62 60/11 30/18 22.01 62 60/11 30/18 22.01 62 60/11 30/18 22.01 62 60/11 30/18 22.01 62 60/11 30/18 22.01 62 60/11 30/18 22.01 63 20/18 63 20/18 7.5 30/18 22.01 63 60/11 30/18 22.01 62 60/11	
228/018 12:26 57 30/01/8 22:31 46 2/91/8 17:41 63 2/91/8 16:46 56 39/01/8 21:51 62 5/91/8 2 288/01 82:13 53 30/01/8 22:36 46 2/91/8 16:46 56 39/01/8 21:51 62 5/91/8 2 288/01 82:136 54 30/01/8 22:46 45 2/91/8 17:51 63 2/91/8 16:56 59 39/01/8 22:01 62 6/91/8 1 288/01 82:15 55 30/01/8 22:56 37 2/91/8 8:01 60 2/91/8 17:16 57 39/01/8 22:16 62 6/91/8 1 288/01 82:16 62 31/01/8 19:01 60 2/91/8 17:16 57 39/01/8 22:16 63 69/01 81 288/01 82:16 61 31/01/8 19:16 61 2/91/8 8:16 59 2/91/8 17:26 59 39/01/8 22:36 62 60/01/8 1 288/01 82:21 61 31/01/8 19:16 61 2/91/8 8:26 61 2/91/8 17:26 59 39/01/8 22:41 62 60/01/8 1 288/01 82:21 61	22:41 60
228/01/8 21:31 5.3 30/01/8 22:36 46 2/91/8 7:41 6.3 2/91/8 16:51 57 3/91/8 21:51 62 5/91/8 288/01/8 21:41 52 30/01/8 22:46 45 2/91/8 7:56 63 2/91/8 16:56 55 3/91/8 22:01 62 6/91/8 1 288/01/8 21:41 55 30/01/8 22:56 37 2/91/8 7:56 63 2/91/8 17:06 57 3/91/8 22:16 62 6/91/8 1 288/01/8 21:56 62 31/01/8 19:01 60 2/91/8 8:16 59 2/91/8 17:11 57 3/91/8 22:16 62 6/91/8 1 288/01/8 22:16 61 31/01/8 19:11 60 2/91/8 8:16 59 2/91/8 17:26 59 3/91/8 22:36 62 6/91/8 1 288/01/8 22:16 61 31/01/8 19:16 61 2/91/8 8:16 59 2/91/8 17:26 59 3/91/8 22:36 62 6/91/8 1 288/01/8 22:16 61 31/01/8 19:21 42 2/91/8 8:36 61 2/91/8 17:36 53 3/91/8 22:46 62	
228/07/8 21/9 141 52 30/07/8 22/01 62 6/07/81 288/07/8 21/51 55 30/07/8 22/51 47 2/9/18 7/50 57 3/9/18 22:01 62 6/07/81 288/07/8 21/51 55 30/07/8 22:56 37 2/9/18 60 2/9/18 17/11 57 3/9/18 22:11 62 69/07/81 288/07/8 22:01 61 31/07/18 19:01 60 2/9/18 61 2/9/18 17/21 57 3/9/18 22:31 62 69/07 288/07 82:22 61 31/07/18 19:26 50 2/9/18 82:1 61 2/9/18 17:26 55 3/9/18 22:36 62 6/9/18 28/07/8 22:26 61 31/07/18 19:36 50 2/9/18 8:36 61 2/9/18 17:46 55 3/9/18 2:2:46 62 6/9/18 2:0/18 12:0/18	22:56 61
$\begin{array}{rrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrrr$	
28/0/16 21:56 62 31/0/18 10:10 20/0/18 17:11 57 30/0/18 22:16 62 60/0/18 28/0/18 22:01 61 31/0/18 19:01 60 20/0/18 17:21 59 30/018 22:31 62 60/018 28/0/18 22:11 61 31/0/18 19:11 60 20/018 17:26 59 30/018 22:33 62 60/018 28/0/18 22:11 61 31/0/18 19:22 61 31/0/18 19:22 61 31/0/18 19:24 62 60/018 28/0/18 22:21 60 31/0/18 19:36 53 20/018 8:31 60 21/0/18 17:46 58 30/018 2:2:46 62 60/018 28/0/18 22:31 60 31/0/18 19:46 55 2/0/18 8:51 52 2/0/18 17:56 59 4/0/18 19:10 62 6/0/18 2/0/18 16:01 <	19:11 56
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	
28/8/18 22:16 61 31/8/18 19:16 61 29/18 17:26 59 30/18 22:31 62 69/18 28/8/18 22:16 61 31/8/18 19:26 61 29/18 17:31 57 39/18 22:41 62 69/18 28/8/18 22:21 60 31/8/18 19:35 29/18 17:41 61 39/18 22:46 62 69/18 28/8/18 22:36 60 31/8/18 19:36 53 29/18 17:46 58 39/18 22:46 62 69/18 28/8/18 22:36 60 31/8/18 19:46 55 29/18 51 52 29/18 16:06 61 49/18 19:06 63 69/18 28/8/18 22:41 60 31/8/18 19:66 55 29/18 16:06 61 49/18 19:16 69/18 29/18 16:06 61 49/18 19:16 69/18 29/18 18:10 <	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	19:36 51
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	19:51 62
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	20:06 64
29/8/18 19.01 67 $31/8/18$ 20.06 57 $29/9/18$ $9:11$ 62 $29/9/18$ $18:16$ 59 $4/9/18$ $19:21$ 55 $6/9/18$ $29/8/18$ $19:06$ 67 $31/8/18$ $20:11$ 55 $29/9/18$ $9:16$ 62 $2/9/18$ $18:21$ 59 $4/9/18$ $19:26$ 62 $6/9/18$ $29/8/18$ $19:16$ 66 $31/8/18$ $20:16$ 55 $2/9/18$ $9:26$ 63 $2/9/18$ $18:36$ 60 $4/9/18$ $19:36$ 57 $6/9/18$ $29/8/18$ $19:26$ 66 $31/8/18$ $20:21$ 54 $2/9/18$ $9:26$ 63 $2/9/18$ $18:31$ 60 $4/9/18$ $19:36$ 57 $6/9/18$ $29/8/18$ $19:26$ 66 $31/8/18$ $20:21$ 54 $2/9/18$ $9:36$ 63 $2/9/18$ $18:31$ 60 $4/9/18$ $19:41$ 56 $6/9/18$ $29/8/18$ $19:26$ 66 $31/8/18$ $20:36$ 56 $2/9/18$ $9:41$ 61 $2/9/18$ $18:46$ 60 $4/9/18$ $19:46$ 61 $6/9/18$ $29/8/18$ $19:36$ 67 $31/8/18$ $20:46$ 54 $2/9/18$ $9:46$ 61 $2/9/18$ $18:51$ 60 $4/9/18$ $20:16$ 56 $6/9/18$ $29/8/18$ $19:46$ 67 $31/8/18$ $20:56$ 53 $2/9/18$ $9:16$ 59 $4/9/18$ $20:16$ 56 $6/9/18$ $29/8/18$ <t< td=""><td>20:16 64</td></t<>	20:16 64
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	20:31 63
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	20:46 64
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	
$\begin{array}{cccccccccccccccccccccccccccccccccccc$	21:01 63
29/8/18 19:56 67 31/8/18 21:01 53 2/9/18 10:06 60 2/9/18 19:11 61 4/9/18 20:16 55 6/9/18 2 29/8/18 20:01 67 31/8/18 21:06 40 2/9/18 10:11 58 2/9/18 19:16 60 4/9/18 20:21 60 6/9/18 2 29/8/18 20:06 67 31/8/18 21:11 61 2/9/18 10:21 58 2/9/18 19:21 64 4/9/18 20:26 53 6/9/18 2 29/8/18 20:16 67 31/8/18 21:16 61 2/9/18 10:21 58 2/9/18 19:26 61 4/9/18 20:31 49 6/9/18 2 29/8/18 20:16 67 31/8/18 21:21 62 2/9/18 10:21 58 2/9/18 19:36 61 4/9/18 20:31 49 6/9/18 2 29/8/18 20:21 67 31/8/18 21:21 62 2/9/18 10:36 58 2/9/18 19:36 64 4/9/18 20:36 46 6/9/18 2 29/8/18 20:31 67 31/8/18 21:31 61 2/9/18 10:36 58 2/9/18 19:41 63 4/9/18 20:46 64	
29/8/18 20:01 67 31/8/18 21:06 40 2/9/18 10:11 58 2/9/18 19:16 60 4/9/18 20:21 60 6/9/18 2 29/8/18 20:06 67 31/8/18 21:11 61 2/9/18 10:16 58 2/9/18 19:21 64 4/9/18 20:26 53 6/9/18 2 29/8/18 20:16 67 31/8/18 21:16 61 2/9/18 10:21 58 2/9/18 19:26 61 4/9/18 20:36 46 6/9/18 2 29/8/18 20:16 67 31/8/18 21:21 62 2/9/18 10:26 61 2/9/18 19:31 60 4/9/18 20:36 46 6/9/18 2 29/8/18 20:21 67 31/8/18 21:26 61 2/9/18 10:31 58 2/9/18 19:36 64 4/9/18 20:41 37 6/9/18 2 29/8/18 20:26 67 31/8/18 21:31 61 2/9/18 10:31 58 2/9/18 19:41 63 4/9/18 20:46 64 6/9/18 2 29/8/18 20:31 67 31/8/18 21:36 61 2/9/18 10:36 58 2/9/18 19:41 63 4/9/18 20:46 64	
29/8/18 20:11 67 31/8/18 21:16 61 2/9/18 10:21 58 2/9/18 19:26 61 4/9/18 20:31 49 6/9/18 20:26 29/8/18 20:16 67 31/8/18 21:21 62 2/9/18 10:26 61 2/9/18 19:31 60 4/9/18 20:36 46 6/9/18 20:26 29/8/18 20:26 67 31/8/18 21:26 61 2/9/18 10:31 58 2/9/18 19:36 64 4/9/18 20:41 37 6/9/18 20:26 29/8/18 20:26 67 31/8/18 21:31 61 2/9/18 10:36 58 2/9/18 19:36 64 4/9/18 20:41 37 6/9/18 20:26 29/8/18 20:26 67 31/8/18 21:31 61 2/9/18 10:36 58 2/9/18 19:41 63 4/9/18 20:46 64 6/9/18 20 29/8/18 20:31 67 31/8/18 21:36 61 2/9/18 10:41 57 2/9/18 19:46 63 4/9/18 20:51 55 6/9/18 20 29/8/18 20:36 67 31/8/18 21:41 61 2/9/18 10:46 56 2/9/18 19:51 63 4/9/18 20:55	21:26 59
29/8/18 20:16 67 31/8/18 21:21 62 2/9/18 10:26 61 2/9/18 19:31 60 4/9/18 20:36 46 6/9/18 20:26 29/8/18 20:21 67 31/8/18 21:26 61 2/9/18 10:31 58 2/9/18 19:36 64 4/9/18 20:41 37 6/9/18 20:21 29/8/18 20:26 67 31/8/18 21:31 61 2/9/18 10:36 58 2/9/18 19:41 63 4/9/18 20:46 64 6/9/18 20:21 29/8/18 20:31 67 31/8/18 21:36 61 2/9/18 10:46 58 2/9/18 19:46 63 4/9/18 20:46 64 6/9/18 20:46 29/8/18 20:36 67 31/8/18 21:36 61 2/9/18 10:46 56 2/9/18 19:51 63 4/9/18 20:56 53 6/9/18 20:51 29/8/18 20:36 67 31/8/18 21:41 61 2/9/18 10:46 56 2/9/18 19:51 63 4/9/18 20:56 53 6/9/18 20:51	
29/8/18 20:26 67 31/8/18 21:31 61 2/9/18 10:36 58 2/9/18 19:41 63 4/9/18 20:46 64 6/9/18 20:42 29/8/18 20:31 67 31/8/18 21:36 61 2/9/18 10:41 57 2/9/18 19:46 63 4/9/18 20:51 55 6/9/18 20:46 29/8/18 20:36 67 31/8/18 21:41 61 2/9/18 10:46 56 2/9/18 19:51 63 4/9/18 20:56 53 6/9/18 20:46 <td< td=""><td>21:41 64</td></td<>	21:41 64
29/8/18 20:31 67 31/8/18 21:36 61 2/9/18 10:41 57 2/9/18 19:46 63 4/9/18 20:51 55 6/9/18 20:20 29/8/18 20:36 67 31/8/18 21:41 61 2/9/18 10:46 56 2/9/18 19:51 63 4/9/18 20:56 53 6/9/18 20	
	21:56 63
20/0/10/20.41 00 01/0/10/21.40 02 12/9/10/10.31 37 12/9/10/19:30 03 4/9/18/21:01 35 0/9/18/2	
29/8/18 20:46 67 31/8/18 21:51 61 2/9/18 10:56 55 2/9/18 20:01 64 4/9/18 21:06 52 6/9/18 20	22:11 60
29/8/18 20:56 68 31/8/18 22:01 61 2/9/18 11:06 56 2/9/18 20:11 63 4/9/18 21:16 64 6/9/18 20	22:21 61
29/8/18 21:01 69 31/8/18 22:06 60 2/9/18 11:11 57 2/9/18 20:16 63 4/9/18 21:21 64 6/9/18 2 29/8/18 21:06 69 31/8/18 22:11 61 2/9/18 11:16 56 2/9/18 20:21 58 4/9/18 21:26 64 6/9/18 20	
29/8/18 21:11 69 31/8/18 22:16 61 2/9/18 11:21 55 2/9/18 20:26 44 4/9/18 21:31 54 6/9/18 20:26	22:36 61
29/8/18 21:16 69 31/8/18 22:21 61 2/9/18 11:26 57 2/9/18 20:31 63 4/9/18 21:36 64 6/9/18 20 29/8/18 21:21 68 31/8/18 22:26 63 2/9/18 11:31 58 2/9/18 20:36 63 4/9/18 21:41 50 6/9/18 20	
29/8/18 21:26 68 31/8/18 22:31 61 2/9/18 11:36 55 2/9/18 20:41 63 4/9/18 21:46 62 6/9/18 20	22:51 61
29/8/18 21:31 69 31/8/18 22:36 61 2/9/18 11:41 58 2/9/18 20:46 63 4/9/18 21:51 60 6/9/18 2 29/8/18 21:36 69 31/8/18 22:41 62 2/9/18 11:46 59 2/9/18 20:51 37 4/9/18 21:56 60 7/9/18 11	
29/8/18 21:41 69 31/8/18 22:46 61 2/9/18 11:51 57 2/9/18 20:56 64 4/9/18 22:01 60 7/9/18 1	19:06 60
29/8/18 21:46 70 31/8/18 22:51 61 2/9/18 11:56 58 2/9/18 21:01 64 4/9/18 22:06 59 7/9/18 1 29/8/18 21:51 69 31/8/18 22:56 60 2/9/18 12:01 58 2/9/18 21:06 64 4/9/18 22:11 60 7/9/18 1	19:16 60
29/8/18 21:56 69 1/9/18 19:01 61 2/9/18 12:06 58 2/9/18 21:11 63 4/9/18 22:16 59 7/9/18 1	19:21 59

7/9/18 19:26 7/9/18 19:31	<u>e Data</u> 60 61	RTN4 (Causeway Bay Communi 9/9/18 8:31 60 9/9/18 8:36 62	9/9/18 17:36 64 9/9/18 17:41 62	10/9/18 22:41 60 10/9/18 22:46 61	13/9/18 19:46 62 13/9/18 19:51 60	15/9/18 20:51 54 15/9/18 20:56 56
7/9/18 19:36	64	9/9/18 8:41 61	9/9/18 17:46 61	10/9/18 22:51 63	13/9/18 19:56 60	15/9/18 21:01 52
7/9/18 19:41	60	9/9/18 8:46 61	9/9/18 17:51 61	10/9/18 22:56 63	13/9/18 20:01 61	15/9/18 21:06 59
7/9/18 19:46	64	9/9/18 8:51 61	9/9/18 17:56 61	11/9/18 19:01 64	13/9/18 20:06 61	15/9/18 21:11 54
7/9/18 19:51	60	9/9/18 8:56 62	9/9/18 18:01 62	11/9/18 19:06 63	13/9/18 20:11 61	15/9/18 21:16 57
7/9/18 19:56	60	9/9/18 9:01 61	9/9/18 18:06 60	11/9/18 19:11 63	13/9/18 20:16 62	15/9/18 21:21 57
7/9/18 20:01	60	9/9/18 9:06 61	9/9/18 18:11 60	11/9/18 19:16 64	13/9/18 20:21 60	15/9/18 21:26 57
7/9/18 20:06	61	9/9/18 9:11 61	9/9/18 18:16 59	11/9/18 19:21 48	13/9/18 20:26 61	15/9/18 21:31 55
7/9/18 20:11	62	9/9/18 9:16 62	9/9/18 18:21 59	11/9/18 19:26 47	13/9/18 20:31 62	15/9/18 21:36 58
7/9/18 20:16	62	9/9/18 9:21 61	9/9/18 18:26 59	11/9/18 19:31 45	13/9/18 20:36 61	15/9/18 21:41 57
7/9/18 20:21	62	9/9/18 9:26 62	9/9/18 18:31 61	11/9/18 19:36 59	13/9/18 20:41 62	15/9/18 21:46 57
7/9/18 20:26	60	9/9/18 9:31 63	9/9/18 18:36 60	11/9/18 19:41 53	13/9/18 20:46 61	15/9/18 21:51 57
7/9/18 20:31	60	9/9/18 9:36 62	9/9/18 18:41 61	11/9/18 19:46 59	13/9/18 20:51 63	15/9/18 21:56 54
7/9/18 20:36	61	9/9/18 9:41 62	9/9/18 18:46 61	11/9/18 19:51 57	13/9/18 20:56 61	15/9/18 22:01 55
7/9/18 20:41	61	9/9/18 9:46 62	9/9/18 18:51 60	11/9/18 19:56 58	13/9/18 21:01 61	15/9/18 22:06 58
7/9/18 20:46	61	9/9/18 9:51 62	9/9/18 18:56 60	11/9/18 20:01 54	13/9/18 21:06 61	15/9/18 22:11 57
7/9/18 20:51	61	9/9/18 9:56 62	9/9/18 19:01 62	11/9/18 20:06 54	13/9/18 21:11 61	15/9/18 22:16 58
7/9/18 20:56	63	9/9/18 10:01 62	9/9/18 19:06 60	11/9/18 20:11 50	13/9/18 21:16 61	15/9/18 22:21 56
7/9/18 21:01	64	9/9/18 10:06 61	9/9/18 19:11 61	11/9/18 20:16 54	13/9/18 21:21 60	15/9/18 22:26 56
7/9/18 21:06	62	9/9/18 10:11 61	9/9/18 19:16 62	11/9/18 20:21 57	13/9/18 21:26 60	15/9/18 22:31 57
7/9/18 21:11	62	9/9/18 10:16 61	9/9/18 19:21 63	11/9/18 20:26 47	13/9/18 21:31 61	15/9/18 22:36 56
7/9/18 21:16	61	9/9/18 10:21 61	9/9/18 19:26 61 9/9/18 19:31 61	11/9/18 20:31 55	13/9/18 21:36 61	15/9/18 22:41 55
7/9/18 21:21	63	9/9/18 10:26 62	9/9/18 19:31 61	11/9/18 20:36 53	13/9/18 21:41 60	15/9/18 22:46 55
7/9/18 21:26	50	9/9/18 10:31 62	9/9/18 19:36 61	11/9/18 20:41 64	13/9/18 21:46 64	15/9/18 22:51 55
7/9/18 21:31	58	9/9/18 10:36 61	9/9/18 19:41 61	11/9/18 20:46 47	13/9/18 21:51 64	15/9/18 22:56 48
7/9/18 21:36	54	9/9/18 10:41 61	9/9/18 19:46 61	11/9/18 20:51 54	13/9/18 21:56 63	16/9/18 7:01 61
7/9/18 21:41	43	9/9/18 10:46 61	9/9/18 19:51 61	11/9/18 20:56 64	13/9/18 22:01 42	16/9/18 7:06 59
7/9/18 21:46	58	9/9/18 10:51 61	9/9/18 19:56 60	11/9/18 21:01 56	13/9/18 22:06 63	16/9/18 7:11 59
7/9/18 21:51	50	9/9/18 10:56 60	9/9/18 20:01 61	11/9/18 21:06 48	13/9/18 22:11 37	16/9/18 7:16 66
7/9/18 21:56	63	9/9/18 11:01 60	9/9/18 20:06 60	11/9/18 21:11 51	13/9/18 22:16 64	16/9/18 7:21 67
7/9/18 22:01	64	9/9/18 11:06 61	9/9/18 20:11 60	11/9/18 21:16 52	13/9/18 22:21 63	16/9/18 7:26 67
7/9/18 22:06	52	9/9/18 11:11 61	9/9/18 20:16 61	11/9/18 21:21 49	13/9/18 22:26 63	16/9/18 7:31 67
7/9/18 22:11	64	9/9/18 11:16 60	9/9/18 20:21 60	11/9/18 21:26 64	13/9/18 22:31 60	16/9/18 7:36 67
7/9/18 22:16	59	9/9/18 11:21 61	9/9/18 20:26 60	11/9/18 21:31 40	13/9/18 22:36 63	16/9/18 7:41 70
7/9/18 22:21	55	9/9/18 11:26 60	9/9/18 20:31 60	11/9/18 21:36 64	13/9/18 22:41 63	16/9/18 7:46 66
7/9/18 22:26	45	9/9/18 11:31 60	9/9/18 20:36 61	11/9/18 21:41 64	13/9/18 22:46 63	16/9/18 7:51 68
7/9/18 22:31	64	9/9/18 11:36 62	9/9/18 20:41 61	11/9/18 21:46 61	13/9/18 22:51 63	16/9/18 7:56 62
7/9/18 22:36	64	9/9/18 11:41 61	9/9/18 20:46 60	11/9/18 21:51 62	13/9/18 22:56 63	16/9/18 8:01 58
7/9/18 22:41	64	9/9/18 11:46 62	9/9/18 20:51 61	11/9/18 21:56 60	14/9/18 19:01 60	16/9/18 8:06 57
7/9/18 22:46	64	9/9/18 11:51 60	9/9/18 20:56 64	11/9/18 22:01 61	14/9/18 19:06 61	16/9/18 8:11 64
7/9/18 22:51	64	9/9/18 11:56 62	9/9/18 21:01 66	11/9/18 22:06 60	14/9/18 19:11 60	16/9/18 8:16 62
7/9/18 22:56	64	9/9/18 12:01 63	9/9/18 21:06 65 0/0/18 21:11 62	11/9/18 22:11 60	14/9/18 19:16 59	16/9/18 8:21 63
8/9/18 19:01	52	9/9/18 12:06 62	9/9/18 21:11 63	11/9/18 22:16 61	14/9/18 19:21 62	16/9/18 8:26 63
8/9/18 19:06	53	9/9/18 12:11 63	9/9/18 21:16 62	11/9/18 22:21 60	14/9/18 19:26 61	16/9/18 8:31 57
8/9/18 19:11	51	9/9/18 12:16 63	9/9/18 21:21 65	11/9/18 22:26 60	14/9/18 19:31 61	16/9/18 8:36 57
8/9/18 19:16	56	9/9/18 12:21 62	9/9/18 21:26 62	11/9/18 22:31 60	14/9/18 19:36 54	16/9/18 8:41 62
8/9/18 19:21	59	9/9/18 12:26 63	9/9/18 21:31 60	11/9/18 22:36 61	14/9/18 19:41 64	16/9/18 8:46 58
8/9/18 19:26	56	9/9/18 12:31 57	9/9/18 21:36 56	11/9/18 22:41 60	14/9/18 19:46 64	16/9/18 8:51 62
8/9/18 19:31	57	9/9/18 12:36 57	9/9/18 21:41 54	11/9/18 22:46 42	14/9/18 19:51 51	16/9/18 8:56 58
8/9/18 19:36	55	9/9/18 12:41 57	9/9/18 21:46 62	11/9/18 22:51 59	14/9/18 19:56 64	16/9/18 9:01 64
8/9/18 19:41	54	9/9/18 12:46 53	9/9/18 21:51 61	11/9/18 22:56 60	14/9/18 20:01 62	16/9/18 9:06 65
8/9/18 19:46	49	9/9/18 12:51 56	9/9/18 21:56 61	12/9/18 19:01 62	14/9/18 20:06 55	16/9/18 9:11 57
8/9/18 19:51	55	9/9/18 12:56 59	9/9/18 22:01 59	12/9/18 19:06 60	14/9/18 20:11 55	16/9/18 9:16 63
8/9/18 19:56	54	9/9/18 13:01 55	9/9/18 22:06 62	12/9/18 19:11 62	14/9/18 20:16 52	16/9/18 9:21 47
8/9/18 20:01	57	9/9/18 13:06 54	9/9/18 22:11 61	12/9/18 19:16 61	14/9/18 20:21 58	16/9/18 9:26 64
8/9/18 20:06	54	9/9/18 13:11 55	9/9/18 22:16 60	12/9/18 19:21 62	14/9/18 20:26 61	16/9/18 9:31 65
8/9/18 20:11	54	9/9/18 13:16 54	9/9/18 22:21 56	12/9/18 19:26 62	14/9/18 20:31 57	16/9/18 9:36 63
8/9/18 20:16	55	9/9/18 13:21 51	9/9/18 22:26 64	12/9/18 19:31 62	14/9/18 20:36 54	16/9/18 9:41 63
8/9/18 20:21	55	9/9/18 13:26 63	9/9/18 22:31 62	12/9/18 19:36 54	14/9/18 20:41 56	16/9/18 9:46 59
8/9/18 20:26	56	9/9/18 13:31 63	9/9/18 22:36 61	12/9/18 19:41 56	14/9/18 20:46 55	16/9/18 9:51 66
8/9/18 20:31	55	9/9/18 13:36 64	9/9/18 22:41 61	12/9/18 19:46 56	14/9/18 20:51 60	16/9/18 9:56 65
8/9/18 20:36	55	9/9/18 13:41 57	9/9/18 22:46 60	12/9/18 19:51 54	14/9/18 20:56 55	16/9/18 10:01 66
8/9/18 20:41	57	9/9/18 13:46 50	9/9/18 22:51 60	12/9/18 19:56 55	14/9/18 21:01 55	16/9/18 10:06 66
8/9/18 20:46	56	9/9/18 13:51 63	9/9/18 22:56 60	12/9/18 20:01 47	14/9/18 21:06 55	16/9/18 10:11 67
8/9/18 20:51	55	9/9/18 13:56 54	10/9/18 19:01 60	12/9/18 20:06 52	14/9/18 21:11 62	16/9/18 10:16 68
8/9/18 20:56	56	9/9/18 14:01 58	10/9/18 19:06 62	12/9/18 20:11 59	14/9/18 21:16 63	16/9/18 10:21 71
8/9/18 21:01	53	9/9/18 14:06 57	10/9/18 19:11 62	12/9/18 20:16 56	14/9/18 21:21 61	16/9/18 10:26 68
8/9/18 21:06	53	9/9/18 14:11 57	10/9/18 19:16 62	12/9/18 20:21 64	14/9/18 21:26 63	16/9/18 10:31 68
8/9/18 21:11	56	9/9/18 14:16 57	10/9/18 19:21 62	12/9/18 20:26 63	14/9/18 21:31 62	16/9/18 10:36 65
8/9/18 21:16	55	9/9/18 14:21 54	10/9/18 19:26 62	12/9/18 20:31 56	14/9/18 21:36 62	16/9/18 10:41 64
8/9/18 21:21	46	9/9/18 14:26 52	10/9/18 19:31 63	12/9/18 20:36 51	14/9/18 21:41 63	16/9/18 10:46 65
8/9/18 21:26	53	9/9/18 14:31 54	10/9/18 19:36 63	12/9/18 20:41 51	14/9/18 21:46 63	16/9/18 10:51 66
8/9/18 21:31	49	9/9/18 14:36 53	10/9/18 19:41 62	12/9/18 20:46 54	14/9/18 21:51 64	16/9/18 10:56 65
8/9/18 21:36	61	9/9/18 14:41 58	10/9/18 19:46 62	12/9/18 20:51 57	14/9/18 21:56 61	16/9/18 11:01 63
8/9/18 21:41	57	9/9/18 14:46 58	10/9/18 19:51 61	12/9/18 20:56 64	14/9/18 22:01 62	16/9/18 11:06 65
8/9/18 21:46	55	9/9/18 14:51 54	10/9/18 19:56 61	12/9/18 21:01 64	14/9/18 22:06 57	16/9/18 11:11 66
8/9/18 21:51	61	9/9/18 14:56 54	10/9/18 20:01 61	12/9/18 21:06 64	14/9/18 22:11 63	16/9/18 11:16 64
8/9/18 21:56	61	9/9/18 15:01 55	10/9/18 20:06 62	12/9/18 21:11 64	14/9/18 22:16 54	16/9/18 11:21 63
8/9/18 22:01	61	9/9/18 15:06 59	10/9/18 20:11 63	12/9/18 21:16 64	14/9/18 22:21 63	16/9/18 11:26 64
8/9/18 22:06	60	9/9/18 15:11 57	10/9/18 20:16 62	12/9/18 21:21 64	14/9/18 22:26 64	16/9/18 11:31 64
8/9/18 22:11	60	9/9/18 15:16 55	10/9/18 20:21 64	12/9/18 21:26 52	14/9/18 22:31 63	16/9/18 11:36 60
8/9/18 22:16	61	9/9/18 15:21 55	10/9/18 20:26 61	12/9/18 21:31 55	14/9/18 22:36 63	16/9/18 11:41 61
8/9/18 22:21	61	9/9/18 15:26 56	10/9/18 20:31 63	12/9/18 21:36 63	14/9/18 22:41 62	16/9/18 11:46 63
8/9/18 22:26	60	9/9/18 15:31 58	10/9/18 20:36 62	12/9/18 21:41 60	14/9/18 22:46 63	16/9/18 11:51 63
8/9/18 22:31	60	9/9/18 15:36 37	10/9/18 20:41 62	12/9/18 21:46 60	14/9/18 22:51 62	16/9/18 11:56 65
8/9/18 22:36	61	9/9/18 15:41 57	10/9/18 20:46 61	12/9/18 21:51 60	14/9/18 22:56 63	16/9/18 12:01 64
8/9/18 22:41	60	9/9/18 15:46 57	10/9/18 20:51 62	12/9/18 21:56 59	15/9/18 19:01 63	16/9/18 12:06 62
8/9/18 22:46	60	9/9/18 15:51 57	10/9/18 20:56 63	12/9/18 22:01 60	15/9/18 19:06 63	
8/9/18 22:51	60	9/9/18 15:51 57	10/9/18 20:56 63	12/9/18 22:01 60	15/9/18 19:06 63	16/9/18 12:11 58
	60	9/9/18 15:56 56	10/9/18 21:01 61	12/9/18 22:06 61	15/9/18 19:11 62	16/9/18 12:16 60
8/9/18 22:56	60	9/9/18 16:01 56	10/9/18 21:06 61	12/9/18 22:11 60	15/9/18 19:16 63	16/9/18 12:21 61
9/9/18 7:01	59	9/9/18 16:06 54	10/9/18 21:11 61	12/9/18 22:16 60	15/9/18 19:21 63	16/9/18 12:26 55
9/9/18 7:06	58	9/9/18 16:11 49	10/9/18 21:16 61	12/9/18 22:21 60	15/9/18 19:26 63	16/9/18 12:31 61
9/9/18 7:11	60	9/9/18 16:16 49	10/9/18 21:21 61	12/9/18 22:26 60	15/9/18 19:31 62	16/9/18 12:36 61
9/9/18 7:16	58	9/9/18 16:21 51	10/9/18 21:26 61	12/9/18 22:31 60	15/9/18 19:36 53	16/9/18 12:41 61
9/9/18 7:21	58	9/9/18 16:26 55	10/9/18 21:31 62	12/9/18 22:36 60	15/9/18 19:41 62	16/9/18 12:46 58
9/9/18 7:26	59	9/9/18 16:31 57	10/9/18 21:36 62	12/9/18 22:41 60	15/9/18 19:46 62	16/9/18 12:51 49
9/9/18 7:31	58	9/9/18 16:36 58	10/9/18 21:41 62	12/9/18 22:46 59	15/9/18 19:51 62	16/9/18 12:56 63
9/9/18 7:36	59	9/9/18 16:41 49	10/9/18 21:46 61	12/9/18 22:51 60	15/9/18 19:56 62	16/9/18 13:01 63
9/9/18 7:41	59	9/9/18 16:46 52	10/9/18 21:51 60	12/9/18 22:56 60	15/9/18 20:01 63	16/9/18 13:06 63
9/9/18 7:46	59	9/9/18 16:51 52	10/9/18 21:56 60	13/9/18 19:01 64	15/9/18 20:06 63	16/9/18 13:11 63
9/9/18 7:51	59	9/9/18 16:56 51	10/9/18 22:01 61	13/9/18 19:06 63	15/9/18 20:11 61	16/9/18 13:16 63
9/9/18 7:56	60	9/9/18 17:01 54	10/9/18 22:06 62	13/9/18 19:11 63	15/9/18 20:16 62	16/9/18 13:21 63
9/9/18 8:01	60	9/9/18 17:06 46	10/9/18 22:11 63	13/9/18 19:16 65	15/9/18 20:21 63	16/9/18 13:26 63
9/9/18 8:06	60	9/9/18 17:11 51	10/9/18 22:16 62	13/9/18 19:21 60	15/9/18 20:26 63	16/9/18 13:31 64
9/9/18 8:11	59	9/9/18 17:16 54	10/9/18 22:21 61	13/9/18 19:26 59	15/9/18 20:31 63	16/9/18 13:36 63
9/9/18 8:16	59	9/9/18 17:21 56	10/9/18 22:26 61	13/9/18 19:31 59	15/9/18 20:36 52	16/9/18 13:41 47
9/9/18 8:21	60	9/9/18 17:26 53	10/9/18 22:31 61	13/9/18 19:36 62	15/9/18 20:41 54	16/9/18 13:46 62
9/9/18 8:26	60	9/9/18 17:31 52	10/9/18 22:36 61	13/9/18 19:41 60	15/9/18 20:46 53	16/9/18 13:51 62

Real-time Noise Data 16/9/18 13:56 50	RTN4 (Causeway Bay Communit 17/9/18 19:01 58	<u>y Centre)</u> 19/9/18 20:06 60	21/9/18 21:11 63	23/9/18 10:16 46	23/9/18 19:21 50
16/9/18 14:01 64	17/9/18 19:06 55	19/9/18 20:11 59	21/9/18 21:16 62	23/9/18 10:16 46	23/9/18 19:26 54
16/9/18 14:06 63	17/9/18 19:11 55	19/9/18 20:16 61	21/9/18 21:21 61	23/9/18 10:26 63	23/9/18 19:31 64
16/9/18 14:11 57 16/9/18 14:16 57	17/9/18 19:16 55 17/9/18 19:21 53	19/9/18 20:21 61 19/9/18 20:26 60	21/9/18 21:26 49 21/9/18 21:31 62	23/9/18 10:31 52 23/9/18 10:36 64	23/9/18 19:36 51 23/9/18 19:41 64
16/9/18 14:21 64	17/9/18 19:26 47	19/9/18 20:31 61	21/9/18 21:36 61	23/9/18 10:41 42	23/9/18 19:46 42
16/9/18 14:26 64 16/9/18 14:31 62	17/9/18 19:31 48 17/9/18 19:36 63	19/9/18 20:36 61 19/9/18 20:41 61	21/9/18 21:41 63 21/9/18 21:46 61	23/9/18 10:46 64 23/9/18 10:51 63	23/9/18 19:51 63 23/9/18 19:56 64
16/9/18 14:36 62	17/9/18 19:41 63	19/9/18 20:46 62	21/9/18 21:51 64	23/9/18 10:56 63	23/9/18 20:01 63
16/9/18 14:41 63 16/9/18 14:46 64	17/9/18 19:46 64 17/9/18 19:51 48	19/9/18 20:51 61 19/9/18 20:56 61	21/9/18 21:56 62 21/9/18 22:01 62	23/9/18 11:01 64 23/9/18 11:06 63	23/9/18 20:06 64 23/9/18 20:11 64
16/9/18 14:51 47	17/9/18 19:56 51	19/9/18 21:01 62	21/9/18 22:06 58	23/9/18 11:11 50	23/9/18 20:16 49
16/9/18 14:56 64 16/9/18 15:01 63	17/9/18 20:01 52 17/9/18 20:06 51	19/9/18 21:06 62 19/9/18 21:11 61	21/9/18 22:11 57 21/9/18 22:16 55	23/9/18 11:16 37 23/9/18 11:21 63	23/9/18 20:21 63 23/9/18 20:26 54
16/9/18 15:06 61	17/9/18 20:00 51	19/9/18 21:16 61	21/9/18 22:21 56	23/9/18 11:26 46	23/9/18 20:31 64
16/9/18 15:11 61	17/9/18 20:16 64	19/9/18 21:21 61	21/9/18 22:26 54	23/9/18 11:31 63	23/9/18 20:36 63
16/9/18 15:16 61 16/9/18 15:21 61	17/9/18 20:21 51 17/9/18 20:26 52	19/9/18 21:26 60 19/9/18 21:31 60	21/9/18 22:31 54 21/9/18 22:36 56	23/9/18 11:36 63 23/9/18 11:41 63	23/9/18 20:41 50 23/9/18 20:46 47
16/9/18 15:26 61	17/9/18 20:31 50	19/9/18 21:36 60	21/9/18 22:41 50	23/9/18 11:46 63	23/9/18 20:51 63
16/9/18 15:31 60 16/9/18 15:36 59	17/9/18 20:36 53 17/9/18 20:41 54	19/9/18 21:41 60 19/9/18 21:46 59	21/9/18 22:46 50 21/9/18 22:51 53	23/9/18 11:51 64 23/9/18 11:56 64	23/9/18 20:56 63 23/9/18 21:01 64
16/9/18 15:41 60	17/9/18 20:46 56	19/9/18 21:51 59	21/9/18 22:56 64	23/9/18 12:01 64	23/9/18 21:06 64
16/9/18 15:46 61 16/9/18 15:51 62	17/9/18 20:51 54 17/9/18 20:56 51	19/9/18 21:56 60 19/9/18 22:01 61	22/9/18 19:01 60 22/9/18 19:06 60	23/9/18 12:06 54 23/9/18 12:11 56	23/9/18 21:11 64 23/9/18 21:16 50
16/9/18 15:56 62	17/9/18 21:01 63	19/9/18 22:06 61	22/9/18 19:11 61	23/9/18 12:16 50	23/9/18 21:21 63
16/9/18 16:01 62 16/9/18 16:06 61	17/9/18 21:06 37 17/9/18 21:11 64	19/9/18 22:11 61 19/9/18 22:16 63	22/9/18 19:16 64 22/9/18 19:21 60	23/9/18 12:21 53 23/9/18 12:26 53	23/9/18 21:26 61 23/9/18 21:31 60
16/9/18 16:11 60	17/9/18 21:16 64	19/9/18 22:21 61	22/9/18 19:26 62	23/9/18 12:31 53	23/9/18 21:36 60
16/9/18 16:16 61	17/9/18 21:21 64	19/9/18 22:26 60	22/9/18 19:31 62	23/9/18 12:36 58	23/9/18 21:41 60
16/9/18 16:21 61 16/9/18 16:26 60	17/9/18 21:26 63 17/9/18 21:31 63	19/9/18 22:31 61 19/9/18 22:36 60	22/9/18 19:36 61 22/9/18 19:41 61	23/9/18 12:41 54 23/9/18 12:46 52	23/9/18 21:46 60 23/9/18 21:51 61
16/9/18 16:31 59	17/9/18 21:36 63	19/9/18 22:41 61	22/9/18 19:46 61	23/9/18 12:51 52	23/9/18 21:56 62
16/9/18 16:36 60 16/9/18 16:41 60	17/9/18 21:41 59 17/9/18 21:46 60	19/9/18 22:46 60 19/9/18 22:51 61	22/9/18 19:51 61 22/9/18 19:56 61	23/9/18 12:56 55 23/9/18 13:01 56	23/9/18 22:01 59 23/9/18 22:06 61
16/9/18 16:46 63	17/9/18 21:51 60	19/9/18 22:56 60	22/9/18 20:01 61	23/9/18 13:06 56	23/9/18 22:11 59
16/9/18 16:51 61 16/9/18 16:56 61	17/9/18 21:56 59 17/9/18 22:01 60	20/9/18 19:01 57 20/9/18 19:06 57	22/9/18 20:06 61 22/9/18 20:11 60	23/9/18 13:11 63 23/9/18 13:16 64	23/9/18 22:16 60 23/9/18 22:21 60
16/9/18 17:01 61	17/9/18 22:06 60	20/9/18 19:11 58	22/9/18 20:16 61	23/9/18 13:10 64	23/9/18 22:26 60
16/9/18 17:06 59	17/9/18 22:11 59	20/9/18 19:16 58	22/9/18 20:21 61	23/9/18 13:26 63	23/9/18 22:31 60
16/9/18 17:11 59 16/9/18 17:16 63	17/9/18 22:16 60 17/9/18 22:21 60	20/9/18 19:21 63 20/9/18 19:26 65	22/9/18 20:26 61 22/9/18 20:31 63	23/9/18 13:31 45 23/9/18 13:36 63	23/9/18 22:36 60 23/9/18 22:41 60
16/9/18 17:21 60	17/9/18 22:26 60	20/9/18 19:31 65	22/9/18 20:36 61	23/9/18 13:41 57	23/9/18 22:46 59
16/9/18 17:26 60 16/9/18 17:31 60	17/9/18 22:31 60 17/9/18 22:36 59	20/9/18 19:36 65 20/9/18 19:41 64	22/9/18 20:41 61 22/9/18 20:46 61	23/9/18 13:46 50 23/9/18 13:51 52	23/9/18 22:51 59 23/9/18 22:56 60
16/9/18 17:36 58	17/9/18 22:41 60	20/9/18 19:46 63	22/9/18 20:51 60	23/9/18 13:56 58	24/9/18 19:01 62
16/9/18 17:41 57 16/9/18 17:46 57	17/9/18 22:46 59 17/9/18 22:51 61	20/9/18 19:51 63 20/9/18 19:56 64	22/9/18 20:56 47 22/9/18 21:01 60	23/9/18 14:01 55 23/9/18 14:06 53	24/9/18 19:06 61 24/9/18 19:11 61
16/9/18 17:51 57	17/9/18 22:56 59	20/9/18 20:01 63	22/9/18 21:06 60	23/9/18 14:11 55	24/9/18 19:16 61
16/9/18 17:56 58	18/9/18 19:01 60	20/9/18 20:06 63	22/9/18 21:11 61	23/9/18 14:16 56	24/9/18 19:21 62
16/9/18 18:01 56 16/9/18 18:06 56	18/9/18 19:06 61 18/9/18 19:11 61	20/9/18 20:11 63 20/9/18 20:16 63	22/9/18 21:16 61 22/9/18 21:21 61	23/9/18 14:21 50 23/9/18 14:26 52	24/9/18 19:26 63 24/9/18 19:31 63
16/9/18 18:11 56	18/9/18 19:16 62	20/9/18 20:21 63	22/9/18 21:26 60	23/9/18 14:31 57	24/9/18 19:36 63
16/9/18 18:16 57 16/9/18 18:21 57	18/9/18 19:21 51 18/9/18 19:26 59	20/9/18 20:26 64 20/9/18 20:31 64	22/9/18 21:31 60 22/9/18 21:36 60	23/9/18 14:36 54 23/9/18 14:41 52	24/9/18 19:41 63 24/9/18 19:46 63
16/9/18 18:26 56	18/9/18 19:31 40	20/9/18 20:36 63	22/9/18 21:41 60	23/9/18 14:46 53	24/9/18 19:51 63
16/9/18 18:31 56 16/9/18 18:36 56	18/9/18 19:36 59 18/9/18 19:41 54	20/9/18 20:41 63 20/9/18 20:46 63	22/9/18 21:46 59 22/9/18 21:51 62	23/9/18 14:51 53 23/9/18 14:56 40	24/9/18 19:56 63 24/9/18 20:01 63
16/9/18 18:41 57	18/9/18 19:46 49	20/9/18 20:51 63	22/9/18 21:56 61	23/9/18 15:01 43	24/9/18 20:06 64
16/9/18 18:46 57 16/9/18 18:51 57	18/9/18 19:51 44 18/9/18 19:56 43	20/9/18 20:56 63 20/9/18 21:01 63	22/9/18 22:01 61 22/9/18 22:06 61	23/9/18 15:06 49 23/9/18 15:11 49	24/9/18 20:11 64 24/9/18 20:16 64
16/9/18 18:56 57	18/9/18 20:01 53	20/9/18 21:06 63	22/9/18 22:11 62	23/9/18 15:16 46	24/9/18 20:21 65
16/9/18 19:01 57	18/9/18 20:06 52	20/9/18 21:11 63 20/9/18 21:16 63	22/9/18 22:16 43 22/9/18 22:21 45	23/9/18 15:21 64	24/9/18 20:26 64
16/9/18 19:06 56 16/9/18 19:11 56	18/9/18 20:11 58 18/9/18 20:16 58	20/9/18 21:16 63 20/9/18 21:21 63	22/9/18 22:26 49	23/9/18 15:26 52 23/9/18 15:31 42	24/9/18 20:31 64 24/9/18 20:36 63
16/9/18 19:16 56	18/9/18 20:21 51	20/9/18 21:26 64	22/9/18 22:31 64	23/9/18 15:36 64	24/9/18 20:41 63
16/9/18 19:21 57 16/9/18 19:26 56	18/9/18 20:26 55 18/9/18 20:31 56	20/9/18 21:31 65 20/9/18 21:36 64	22/9/18 22:36 58 22/9/18 22:41 64	23/9/18 15:41 64 23/9/18 15:46 47	24/9/18 20:46 65 24/9/18 20:51 64
16/9/18 19:31 58	18/9/18 20:36 45	20/9/18 21:41 63	22/9/18 22:46 63	23/9/18 15:51 55	24/9/18 20:56 64
16/9/18 19:36 59 16/9/18 19:41 57	18/9/18 20:41 40 18/9/18 20:46 47	20/9/18 21:46 58 20/9/18 21:51 59	22/9/18 22:51 64 22/9/18 22:56 64	23/9/18 15:56 56 23/9/18 16:01 58	24/9/18 21:01 63 24/9/18 21:06 63
16/9/18 19:46 57	18/9/18 20:51 57	20/9/18 21:56 59	23/9/18 7:01 63	23/9/18 16:06 53	24/9/18 21:11 63
16/9/18 19:51 58 16/9/18 19:56 60	18/9/18 20:56 59 18/9/18 21:01 59	20/9/18 22:01 58 20/9/18 22:06 62	23/9/18 7:06 63 23/9/18 7:11 59	23/9/18 16:11 56 23/9/18 16:16 56	24/9/18 21:16 63 24/9/18 21:21 64
16/9/18 20:01 55	18/9/18 21:06 57	20/9/18 22:11 57	23/9/18 7:16 63	23/9/18 16:21 57	24/9/18 21:26 65
16/9/18 20:06 54	18/9/18 21:11 64 18/9/18 21:16 55	20/9/18 22:16 58	23/9/18 7:21 64	23/9/18 16:26 60	24/9/18 21:31 65
16/9/18 20:11 63 16/9/18 20:16 61	18/9/18 21:16 55 18/9/18 21:21 45	20/9/18 22:21 59 20/9/18 22:26 63	23/9/18 7:26 63 23/9/18 7:31 63	23/9/18 16:31 61 23/9/18 16:36 51	24/9/18 21:36 66 24/9/18 21:41 65
16/9/18 20:21 62	18/9/18 21:26 57	20/9/18 22:31 59	23/9/18 7:36 63	23/9/18 16:41 55	24/9/18 21:46 65
16/9/18 20:26 61 16/9/18 20:31 62	18/9/18 21:31 50 18/9/18 21:36 50	20/9/18 22:36 59 20/9/18 22:41 58	23/9/18 7:41 60 23/9/18 7:46 60	23/9/18 16:46 58 23/9/18 16:51 62	24/9/18 21:51 65 24/9/18 21:56 65
16/9/18 20:36 61	18/9/18 21:41 51	20/9/18 22:46 59	23/9/18 7:51 60	23/9/18 16:56 54	24/9/18 22:01 66
16/9/18 20:41 61 16/9/18 20:46 61	18/9/18 21:46 49 18/9/18 21:51 64	20/9/18 22:51 59 20/9/18 22:56 59	23/9/18 7:56 60 23/9/18 8:01 61	23/9/18 17:01 58 23/9/18 17:06 54	24/9/18 22:06 66 24/9/18 22:11 66
16/9/18 20:51 61	18/9/18 21:56 62	21/9/18 19:01 60	23/9/18 8:06 60	23/9/18 17:11 57	24/9/18 22:16 66
16/9/18 20:56 60 16/9/18 21:01 60	18/9/18 22:01 54 18/9/18 22:06 61	21/9/18 19:06 63 21/9/18 19:11 60	23/9/18 8:11 60 23/9/18 8:16 60	23/9/18 17:16 55 23/9/18 17:21 56	24/9/18 22:21 65 24/9/18 22:26 65
16/9/18 21:06 60	18/9/18 22:11 61	21/9/18 19:16 60	23/9/18 8:21 61	23/9/18 17:26 56	24/9/18 22:31 66
16/9/18 21:11 60	18/9/18 22:16 60	21/9/18 19:21 61	23/9/18 8:26 60	23/9/18 17:31 53	24/9/18 22:36 65
16/9/18 21:16 61 16/9/18 21:21 60	18/9/18 22:21 60 18/9/18 22:26 60	21/9/18 19:26 60 21/9/18 19:31 47	23/9/18 8:31 60 23/9/18 8:36 60	23/9/18 17:36 57 23/9/18 17:41 43	24/9/18 22:41 65 24/9/18 22:46 65
16/9/18 21:26 59	18/9/18 22:31 60	21/9/18 19:36 64	23/9/18 8:41 61	23/9/18 17:46 52	24/9/18 22:51 65
16/9/18 21:31 58 16/9/18 21:36 61	18/9/18 22:36 59 18/9/18 22:41 61	21/9/18 19:41 54 21/9/18 19:46 50	23/9/18 8:46 60 23/9/18 8:51 60	23/9/18 17:51 51 23/9/18 17:56 56	24/9/18 22:56 65 25/9/18 7:01 61
16/9/18 21:41 58	18/9/18 22:46 60	21/9/18 19:51 48	23/9/18 8:56 61	23/9/18 18:01 52	25/9/18 7:06 62
16/9/18 21:46 59 16/9/18 21:51 59	18/9/18 22:51 60 18/9/18 22:56 59	21/9/18 19:56 55 21/9/18 20:01 50	23/9/18 9:01 61 23/9/18 9:06 60	23/9/18 18:06 56 23/9/18 18:11 43	25/9/18 7:11 62 25/9/18 7:16 62
16/9/18 21:56 60	19/9/18 19:01 62	21/9/18 20:06 54	23/9/18 9:11 58	23/9/18 18:16 52	25/9/18 7:21 61
16/9/18 22:01 60	19/9/18 19:06 62	21/9/18 20:11 59	23/9/18 9:16 63	23/9/18 18:21 53	25/9/18 7:26 62
16/9/18 22:06 59 16/9/18 22:11 59	19/9/18 19:11 61 19/9/18 19:16 61	21/9/18 20:16 50 21/9/18 20:21 53	23/9/18 9:21 60 23/9/18 9:26 55	23/9/18 18:26 53 23/9/18 18:31 49	25/9/18 7:31 62 25/9/18 7:36 62
16/9/18 22:16 59	19/9/18 19:21 61	21/9/18 20:26 45	23/9/18 9:31 56	23/9/18 18:36 48	25/9/18 7:41 63
16/9/18 22:21 59 16/9/18 22:26 59	19/9/18 19:26 61 19/9/18 19:31 61	21/9/18 20:31 55 21/9/18 20:36 54	23/9/18 9:36 58 23/9/18 9:41 54	23/9/18 18:41 49 23/9/18 18:46 50	25/9/18 7:46 62 25/9/18 7:51 61
16/9/18 22:31 59	19/9/18 19:36 61	21/9/18 20:41 44	23/9/18 9:46 55	23/9/18 18:51 56	25/9/18 7:56 60
16/9/18 22:36 58 16/9/18 22:41 57	19/9/18 19:41 63 19/9/18 19:46 61	21/9/18 20:46 52 21/9/18 20:51 60	23/9/18 9:51 53 23/9/18 9:56 51	23/9/18 18:56 43 23/9/18 19:01 60	25/9/18 8:01 59 25/9/18 8:06 60
16/9/18 22:46 57	19/9/18 19:51 60	21/9/18 20:56 57	23/9/18 10:01 55	23/9/18 19:06 54	25/9/18 8:11 59
16/9/18 22:51 57	19/9/18 19:56 60	21/9/18 21:01 56	23/9/18 10:06 55	23/9/18 19:11 54	25/9/18 8:16 61
16/9/18 22:56 57	19/9/18 20:01 61	21/9/18 21:06 55	23/9/18 10:11 55	23/9/18 19:16 37	25/9/18 8:21 61

Real-time Noise Data	RTN4 (Causeway Bay Communi	v Centre)			
25/9/18 8:26 60	25/9/18 17:31 62	26/9/18 22:36 60	28/8/18 0:26 61	29/8/18 1:31 57	30/8/18 2:36 67
25/9/18 8:31 60 25/9/18 8:36 60	25/9/18 17:36 62 25/9/18 17:41 62	26/9/18 22:41 60 26/9/18 22:46 60	28/8/18 0:31 60 28/8/18 0:36 59	29/8/18 1:36 56 29/8/18 1:41 57	30/8/18 2:41 67 30/8/18 2:46 68
25/9/18 8:41 62	25/9/18 17:46 63	26/9/18 22:51 59	28/8/18 0:41 61	29/8/18 1:46 56	30/8/18 2:51 67
25/9/18 8:46 62 25/9/18 8:51 63	25/9/18 17:51 62 25/9/18 17:56 62	26/9/18 22:56 60	28/8/18 0:46 69 28/8/18 0:51 70	29/8/18 1:51 56 29/8/18 1:56 56	30/8/18 2:56 66 30/8/18 3:01 66
25/9/18 8:56 63	25/9/18 18:01 63	Night time: 23:00-07:00	28/8/18 0:56 67	29/8/18 2:01 56	30/8/18 3:06 67
25/9/18 9:01 61 25/9/18 9:06 63	25/9/18 18:06 62 25/9/18 18:11 62	27/8/18 0:01 64	28/8/18 1:01 65 28/8/18 1:06 69	29/8/18 2:06 56 29/8/18 2:11 57	30/8/18 3:11 66 30/8/18 3:16 65
25/9/18 9:11 62	25/9/18 18:16 62	27/8/18 0:06 62	28/8/18 1:11 66	29/8/18 2:16 57	30/8/18 3:21 65
25/9/18 9:16 62 25/9/18 9:21 61	25/9/18 18:21 62 25/9/18 18:26 62	27/8/18 0:11 64 27/8/18 0:16 62	28/8/18 1:16 62 28/8/18 1:21 63	29/8/18 2:21 55 29/8/18 2:26 56	30/8/18 3:26 65 30/8/18 3:31 64
25/9/18 9:26 62	25/9/18 18:31 62	27/8/18 0:21 63	28/8/18 1:26 63	29/8/18 2:31 56	30/8/18 3:36 64
25/9/18 9:31 61 25/9/18 9:36 61	25/9/18 18:36 62 25/9/18 18:41 62	27/8/18 0:26 63 27/8/18 0:31 62	28/8/18 1:31 61 28/8/18 1:36 58	29/8/18 2:36 55 29/8/18 2:41 56	30/8/18 3:41 65 30/8/18 3:46 64
25/9/18 9:41 61	25/9/18 18:46 63	27/8/18 0:36 62	28/8/18 1:41 60	29/8/18 2:46 56	30/8/18 3:51 63
25/9/18 9:46 62 25/9/18 9:51 62	25/9/18 18:51 62 25/9/18 18:56 63	27/8/18 0:41 62 27/8/18 0:46 61	28/8/18 1:46 55 28/8/18 1:51 59	29/8/18 2:51 55 29/8/18 2:56 55	30/8/18 3:56 64 30/8/18 4:01 64
25/9/18 9:56 62	25/9/18 19:01 62	27/8/18 0:51 60	28/8/18 1:56 57	29/8/18 3:01 55	30/8/18 4:06 64
25/9/18 10:01 62 25/9/18 10:06 60	25/9/18 19:06 62 25/9/18 19:11 62	27/8/18 0:56 60 27/8/18 1:01 56	28/8/18 2:01 57 28/8/18 2:06 55	29/8/18 3:06 56 29/8/18 3:11 56	30/8/18 4:11 63 30/8/18 4:16 64
25/9/18 10:11 59	25/9/18 19:16 62	27/8/18 1:06 59	28/8/18 2:11 55	29/8/18 3:16 56	30/8/18 4:21 64
25/9/18 10:16 53 25/9/18 10:21 58	25/9/18 19:21 62 25/9/18 19:26 62	27/8/18 1:11 57 27/8/18 1:16 56	28/8/18 2:16 55 28/8/18 2:21 53	29/8/18 3:21 55 29/8/18 3:26 55	30/8/18 4:26 65 30/8/18 4:31 63
25/9/18 10:26 56	25/9/18 19:31 62	27/8/18 1:21 58	28/8/18 2:26 54	29/8/18 3:31 56	30/8/18 4:36 63
25/9/18 10:31 54 25/9/18 10:36 56	25/9/18 19:36 62 25/9/18 19:41 63	27/8/18 1:26 56 27/8/18 1:31 55	28/8/18 2:31 54 28/8/18 2:36 52	29/8/18 3:36 64 29/8/18 3:41 62	30/8/18 4:41 64 30/8/18 4:46 65
25/9/18 10:41 57	25/9/18 19:46 62	27/8/18 1:36 56	28/8/18 2:41 53	29/8/18 3:46 60	30/8/18 4:51 64
25/9/18 10:46 57 25/9/18 10:51 54	25/9/18 19:51 62 25/9/18 19:56 62	27/8/18 1:41 56 27/8/18 1:46 55	28/8/18 2:46 56 28/8/18 2:51 55	29/8/18 3:51 58 29/8/18 3:56 56	30/8/18 4:56 63 30/8/18 5:01 64
25/9/18 10:56 53	25/9/18 20:01 62	27/8/18 1:51 57	28/8/18 2:56 55	29/8/18 4:01 56	30/8/18 5:06 63
25/9/18 11:01 53 25/9/18 11:06 43	25/9/18 20:06 62 25/9/18 20:11 63	27/8/18 1:56 56 27/8/18 2:01 58	28/8/18 3:01 63 28/8/18 3:06 66	29/8/18 4:06 55 29/8/18 4:11 55	30/8/18 5:11 63 30/8/18 5:16 64
25/9/18 11:11 56	25/9/18 20:16 62	27/8/18 2:06 58	28/8/18 3:11 62	29/8/18 4:16 56	30/8/18 5:21 64
25/9/18 11:16 55 25/9/18 11:21 56	25/9/18 20:21 62 25/9/18 20:26 63	27/8/18 2:11 54 27/8/18 2:16 52	28/8/18 3:16 52 28/8/18 3:21 59	29/8/18 4:21 56 29/8/18 4:26 56	30/8/18 5:26 64 30/8/18 5:31 63
25/9/18 11:26 54	25/9/18 20:31 62	27/8/18 2:21 56	28/8/18 3:26 47	29/8/18 4:31 56	30/8/18 5:36 64
25/9/18 11:31 56 25/9/18 11:36 57	25/9/18 20:36 62 25/9/18 20:41 62	27/8/18 2:26 55 27/8/18 2:31 57	28/8/18 3:31 56 28/8/18 3:36 59	29/8/18 4:36 55 29/8/18 4:41 56	30/8/18 5:41 64 30/8/18 5:46 64
25/9/18 11:41 54	25/9/18 20:46 62	27/8/18 2:36 56	28/8/18 3:41 59	29/8/18 4:46 56	30/8/18 5:51 64
25/9/18 11:46 53 25/9/18 11:51 50	25/9/18 20:51 62 25/9/18 20:56 62	27/8/18 2:41 57 27/8/18 2:46 54	28/8/18 3:46 58 28/8/18 3:51 58	29/8/18 4:51 56 29/8/18 4:56 56	30/8/18 5:56 65 30/8/18 6:01 64
25/9/18 11:56 53	25/9/18 21:01 62	27/8/18 2:51 55	28/8/18 3:56 59	29/8/18 5:01 55	30/8/18 6:06 65
25/9/18 12:01 53 25/9/18 12:06 53	25/9/18 21:06 62 25/9/18 21:11 62	27/8/18 2:56 55 27/8/18 3:01 56	28/8/18 4:01 59 28/8/18 4:06 60	29/8/18 5:06 56 29/8/18 5:11 56	30/8/18 6:11 65 30/8/18 6:16 66
25/9/18 12:11 51	25/9/18 21:16 63	27/8/18 3:06 56	28/8/18 4:11 59	29/8/18 5:16 58	30/8/18 6:21 65
25/9/18 12:16 56 25/9/18 12:21 55	25/9/18 21:21 62 25/9/18 21:26 62	27/8/18 3:11 53 27/8/18 3:16 54	28/8/18 4:16 48 28/8/18 4:21 60	29/8/18 5:21 56 29/8/18 5:26 57	30/8/18 6:26 65 30/8/18 6:31 66
25/9/18 12:26 61	25/9/18 21:31 62	27/8/18 3:21 55	28/8/18 4:26 60	29/8/18 5:31 56	30/8/18 6:36 66
25/9/18 12:31 57 25/9/18 12:36 56	25/9/18 21:36 62 25/9/18 21:41 62	27/8/18 3:26 51 27/8/18 3:31 54	28/8/18 4:31 58 28/8/18 4:36 58	29/8/18 5:36 57 29/8/18 5:41 57	30/8/18 6:41 65 30/8/18 6:46 65
25/9/18 12:41 53	25/9/18 21:46 62	27/8/18 3:36 55	28/8/18 4:41 59	29/8/18 5:46 58	30/8/18 6:51 65
25/9/18 12:46 54 25/9/18 12:51 56	25/9/18 21:51 63 25/9/18 21:56 62	27/8/18 3:41 53 27/8/18 3:46 56	28/8/18 4:46 59 28/8/18 4:51 59	29/8/18 5:51 57 29/8/18 5:56 58	30/8/18 6:56 66 30/8/18 23:01 61
25/9/18 12:56 53	25/9/18 22:01 62	27/8/18 3:51 50	28/8/18 4:56 59	29/8/18 6:01 57	30/8/18 23:06 60
25/9/18 13:01 55 25/9/18 13:06 57	25/9/18 22:06 62 25/9/18 22:11 63	27/8/18 3:56 50 27/8/18 4:01 38	28/8/18 5:01 59 28/8/18 5:06 59	29/8/18 6:06 58 29/8/18 6:11 58	30/8/18 23:11 60 30/8/18 23:16 61
25/9/18 13:11 54	25/9/18 22:16 62	27/8/18 4:06 41	28/8/18 5:11 59	29/8/18 6:16 59	30/8/18 23:21 60
25/9/18 13:16 53 25/9/18 13:21 56	25/9/18 22:21 62 25/9/18 22:26 63	27/8/18 4:11 60 27/8/18 4:16 61	28/8/18 5:16 61 28/8/18 5:21 60	29/8/18 6:21 60 29/8/18 6:26 60	30/8/18 23:26 65 30/8/18 23:31 67
25/9/18 13:26 54	25/9/18 22:31 63	27/8/18 4:21 47	28/8/18 5:26 60	29/8/18 6:31 60	30/8/18 23:36 67
25/9/18 13:31 46 25/9/18 13:36 54	25/9/18 22:36 63 25/9/18 22:41 57	27/8/18 4:26 51 27/8/18 4:31 51	28/8/18 5:31 60 28/8/18 5:36 46	29/8/18 6:36 60 29/8/18 6:41 61	30/8/18 23:41 67 30/8/18 23:46 66
25/9/18 13:41 56	25/9/18 22:46 62	27/8/18 4:36 61	28/8/18 5:41 59	29/8/18 6:46 61	30/8/18 23:51 65
25/9/18 13:46 57 25/9/18 13:51 56	25/9/18 22:51 62 25/9/18 22:56 62	27/8/18 4:41 52 27/8/18 4:46 50	28/8/18 5:46 60 28/8/18 5:51 61	29/8/18 6:51 42 29/8/18 6:56 52	30/8/18 23:56 66 31/8/18 0:01 67
25/9/18 13:56 50	26/9/18 19:01 61	27/8/18 4:51 51	28/8/18 5:56 48	29/8/18 23:01 69	31/8/18 0:06 66
25/9/18 14:01 60 25/9/18 14:06 50	26/9/18 19:06 59 26/9/18 19:11 64	27/8/18 4:56 53 27/8/18 5:01 49	28/8/18 6:01 61 28/8/18 6:06 56	29/8/18 23:06 69 29/8/18 23:11 68	31/8/18 0:11 66 31/8/18 0:16 66
25/9/18 14:11 51	26/9/18 19:16 51	27/8/18 5:06 51	28/8/18 6:11 57	29/8/18 23:16 69	31/8/18 0:21 66
25/9/18 14:16 64 25/9/18 14:21 54	26/9/18 19:21 53 26/9/18 19:26 51	27/8/18 5:11 55 27/8/18 5:16 54	28/8/18 6:16 57 28/8/18 6:21 59	29/8/18 23:21 70 29/8/18 23:26 69	31/8/18 0:26 65 31/8/18 0:31 64
25/9/18 14:26 51	26/9/18 19:31 54	27/8/18 5:21 56	28/8/18 6:26 61	29/8/18 23:31 68	31/8/18 0:36 64
25/9/18 14:31 64 25/9/18 14:36 63	26/9/18 19:36 58 26/9/18 19:41 59	27/8/18 5:26 56 27/8/18 5:31 55	28/8/18 6:31 60 28/8/18 6:36 61	29/8/18 23:36 69 29/8/18 23:41 69	31/8/18 0:41 65 31/8/18 0:46 62
25/9/18 14:41 51	26/9/18 19:46 57	27/8/18 5:36 57	28/8/18 6:41 61	29/8/18 23:46 69	31/8/18 0:51 61
25/9/18 14:46 53 25/9/18 14:51 56	26/9/18 19:51 56 26/9/18 19:56 56	27/8/18 5:41 57 27/8/18 5:46 58	28/8/18 6:46 62 28/8/18 6:51 63	29/8/18 23:51 69 29/8/18 23:56 68	31/8/18 0:56 62 31/8/18 1:01 63
25/9/18 14:56 56 25/9/18 15:01 54	26/9/18 20:01 55 26/9/18 20:06 54	27/8/18 5:51 60	28/8/18 6:56 63 28/8/18 23:01 60	30/8/18 0:01 68 30/8/18 0:06 69	31/8/18 1:06 60
25/9/18 15:01 54 25/9/18 15:06 49	26/9/18 20:06 54 26/9/18 20:11 55	27/8/18 5:56 59 27/8/18 6:01 59	28/8/18 23:01 60 28/8/18 23:06 60	30/8/18 0:06 69 30/8/18 0:11 69	31/8/18 1:11 60 31/8/18 1:16 62
25/9/18 15:11 64 25/9/18 15:16 52	26/9/18 20:16 57 26/0/18 20:21 58	27/8/18 6:06 59	28/8/18 23:11 60 28/8/18 23:16 60	30/8/18 0:16 69	31/8/18 1:21 60
25/9/18 15:16 52 25/9/18 15:21 44	26/9/18 20:21 58 26/9/18 20:26 57	27/8/18 6:11 60 27/8/18 6:16 61	28/8/18 23:16 60 28/8/18 23:21 60	30/8/18 0:21 69 30/8/18 0:26 69	31/8/18 1:26 55 31/8/18 1:31 55
25/9/18 15:26 55 25/9/18 15:31 54	26/9/18 20:31 56 26/9/18 20:36 56	27/8/18 6:21 61	28/8/18 23:26 60	30/8/18 0:31 69	31/8/18 1:36 60
25/9/18 15:31 54 25/9/18 15:36 61	26/9/18 20:36 56 26/9/18 20:41 56	27/8/18 6:26 62 27/8/18 6:31 63	28/8/18 23:31 60 28/8/18 23:36 60	30/8/18 0:36 68 30/8/18 0:41 69	31/8/18 1:41 59 31/8/18 1:46 52
25/9/18 15:41 62	26/9/18 20:46 51	27/8/18 6:36 63	28/8/18 23:41 59	30/8/18 0:46 69	31/8/18 1:51 53
25/9/18 15:46 61 25/9/18 15:51 61	26/9/18 20:51 49 26/9/18 20:56 48	27/8/18 6:41 64 27/8/18 6:46 64	28/8/18 23:46 59 28/8/18 23:51 59	30/8/18 0:51 69 30/8/18 0:56 68	31/8/18 1:56 59 31/8/18 2:01 58
25/9/18 15:56 62	26/9/18 21:01 51	27/8/18 6:51 64	28/8/18 23:56 59	30/8/18 1:01 68	31/8/18 2:06 53
25/9/18 16:06 63	26/9/18 21:11 53	27/8/18 23:01 64	29/8/18 0:06 58	30/8/18 1:11 69	31/8/18 2:16 58
25/9/18 16:11 63 25/9/18 16:16 63	26/9/18 21:16 64 26/9/18 21:21 40	27/8/18 23:06 63 27/8/18 23:11 63	29/8/18 0:11 59 29/8/18 0:16 58	30/8/18 1:16 68 30/8/18 1:21 68	31/8/18 2:21 59 31/8/18 2:26 52
25/9/18 16:21 62	26/9/18 21:26 52	27/8/18 23:16 62	29/8/18 0:21 58	30/8/18 1:26 69	31/8/18 2:31 51
25/9/18 16:26 62 25/9/18 16:31 62	26/9/18 21:31 50 26/9/18 21:36 52	27/8/18 23:21 63 27/8/18 23:26 63	29/8/18 0:26 59 29/8/18 0:31 59	30/8/18 1:31 69 30/8/18 1:36 69	31/8/18 2:36 58 31/8/18 2:41 59
25/9/18 16:36 63	26/9/18 21:41 54	27/8/18 23:31 64	29/8/18 0:36 58	30/8/18 1:41 69	31/8/18 2:46 48
25/9/18 16:41 63 25/9/18 16:46 63	26/9/18 21:46 48 26/9/18 21:51 63	27/8/18 23:36 62 27/8/18 23:41 62	29/8/18 0:41 58 29/8/18 0:46 60	30/8/18 1:46 68 30/8/18 1:51 68	31/8/18 2:51 51 31/8/18 2:56 58
25/9/18 16:51 62	26/9/18 21:56 59	27/8/18 23:46 62	29/8/18 0:51 58	30/8/18 1:56 69	31/8/18 3:01 58
25/9/18 16:56 62 25/9/18 17:01 63	26/9/18 22:01 60 26/9/18 22:06 61	27/8/18 23:51 61 27/8/18 23:56 61	29/8/18 0:56 59 29/8/18 1:01 58	30/8/18 2:01 69 30/8/18 2:06 68	31/8/18 3:06 46 31/8/18 3:11 45
25/9/18 17:06 63	26/9/18 22:11 60	28/8/18 0:01 60	29/8/18 1:06 58	30/8/18 2:11 68	31/8/18 3:16 57
25/9/18 17:11 63 25/9/18 17:16 62	26/9/18 22:16 60 26/9/18 22:21 60	28/8/18 0:06 60 28/8/18 0:11 62	29/8/18 1:11 57 29/8/18 1:16 57	30/8/18 2:16 68 30/8/18 2:21 68	31/8/18 3:21 59 31/8/18 3:26 52
25/9/18 17:21 62	26/9/18 22:26 60	28/8/18 0:16 60	29/8/18 1:21 57	30/8/18 2:26 68	31/8/18 3:31 53
25/9/18 17:26 59	26/9/18 22:31 60	28/8/18 0:21 60	29/8/18 1:26 57	30/8/18 2:31 68	31/8/18 3:36 59

31/8/18 3:41	Data 57	RTN4 (Causeway Bay Comn 1/9/18 4:46 56	2/9/18 5:51 57	3/9/18 6:56 60	5/9/18 0:01 59	6/9/18 1:06 58
31/8/18 3:46	61	1/9/18 4:51 56	2/9/18 5:56 56	3/9/18 23:01 56	5/9/18 0:06 58	6/9/18 1:11 58
31/8/18 3:51	51	1/9/18 4:56 57	2/9/18 6:01 56	3/9/18 23:06 55	5/9/18 0:11 59	6/9/18 1:16 58
31/8/18 3:56	60	1/9/18 5:01 56	2/9/18 6:06 58	3/9/18 23:11 57	5/9/18 0:16 58	6/9/18 1:21 58
31/8/18 4:01	49	1/9/18 5:06 56	2/9/18 6:11 56	3/9/18 23:16 57	5/9/18 0:21 59	6/9/18 1:26 57
31/8/18 4:06	49 35	1/9/18 5:11 58	2/9/18 6:16 60	3/9/18 23:21 56	5/9/18 0:26 60	6/9/18 1:31 58
31/8/18 4:11	56	1/9/18 5:16 56	2/9/18 6:21 57	3/9/18 23:26 56	5/9/18 0:31 59	6/9/18 1:36 58
31/8/18 4:16	58	1/9/18 5:21 56	2/9/18 6:26 57	3/9/18 23:31 56	5/9/18 0:36 58	6/9/18 1:41 57
31/8/18 4:21	55	1/9/18 5:26 58	2/9/18 6:31 58	3/9/18 23:36 56	5/9/18 0:41 58	6/9/18 1:46 57
31/8/18 4:26	50	1/9/18 5:31 57	2/9/18 6:36 58	3/9/18 23:41 55	5/9/18 0:46 57	6/9/18 1:51 58
31/8/18 4:31	56	1/9/18 5:36 56	2/9/18 6:41 58	3/9/18 23:46 55	5/9/18 0:51 58	6/9/18 1:56 57
31/8/18 4:36	59	1/9/18 5:41 57	2/9/18 6:46 58	3/9/18 23:51 55	5/9/18 0:56 58	6/9/18 2:01 58
31/8/18 4:41	55	1/9/18 5:46 58	2/9/18 6:51 58	3/9/18 23:56 51	5/9/18 1:01 57	6/9/18 2:06 57
31/8/18 4:46	61	1/9/18 5:51 57	2/9/18 6:56 58	4/9/18 0:01 49	5/9/18 1:06 57	6/9/18 2:11 57
31/8/18 4:51	57	1/9/18 5:56 57	2/9/18 23:01 57	4/9/18 0:06 51	5/9/18 1:11 59	6/9/18 2:16 57
31/8/18 4:56	58	1/9/18 6:01 58	2/9/18 23:06 55	4/9/18 0:11 54	5/9/18 1:16 57	6/9/18 2:21 57
31/8/18 5:01	50	1/9/18 6:06 58	2/9/18 23:11 56	4/9/18 0:16 53	5/9/18 1:21 56	6/9/18 2:26 57
31/8/18 5:06	50	1/9/18 6:11 57	2/9/18 23:16 56	4/9/18 0:21 54	5/9/18 1:26 57	6/9/18 2:31 57
31/8/18 5:11	56	1/9/18 6:16 58	2/9/18 23:21 55	4/9/18 0:26 52	5/9/18 1:31 57	6/9/18 2:36 57
31/8/18 5:16	59	1/9/18 6:21 59	2/9/18 23:26 57	4/9/18 0:31 49	5/9/18 1:36 56	6/9/18 2:41 57
31/8/18 5:21	51	1/9/18 6:26 56	2/9/18 23:31 56	4/9/18 0:36 59	5/9/18 1:41 56	6/9/18 2:46 57
31/8/18 5:26	49	1/9/18 6:31 55	2/9/18 23:36 55	4/9/18 0:41 53	5/9/18 1:46 57	6/9/18 2:51 57
31/8/18 5:31	47	1/9/18 6:36 61	2/9/18 23:41 56	4/9/18 0:46 44	5/9/18 1:51 57	6/9/18 2:56 57
31/8/18 5:36	55	1/9/18 6:41 61	2/9/18 23:46 56	4/9/18 0:51 49	5/9/18 1:56 56	6/9/18 3:01 57
31/8/18 5:41	57	1/9/18 6:46 60	2/9/18 23:51 55	4/9/18 0:56 46	5/9/18 2:01 56	6/9/18 3:06 57
31/8/18 5:46	57	1/9/18 6:51 60	2/9/18 23:56 58	4/9/18 1:01 45	5/9/18 2:06 56	6/9/18 3:11 56
31/8/18 5:51	47	1/9/18 6:56 60	3/9/18 0:01 54	4/9/18 1:06 46	5/9/18 2:11 56	6/9/18 3:16 57
31/8/18 5:56	53	1/9/18 23:01 61	3/9/18 0:06 57	4/9/18 1:11 35	5/9/18 2:16 56	6/9/18 3:21 56
31/8/18 6:01	55	1/9/18 23:06 60 1/9/18 23:11 60	3/9/18 0:11 59	4/9/18 1:16 49 4/9/18 1:21 44	5/9/18 2:21 56 5/9/18 2:26 57	6/9/18 3:26 57
31/8/18 6:06	58	1/9/18 23:11 60	3/9/18 0:16 55	4/9/18 1:21 44	5/9/18 2:31 56	6/9/18 3:31 58
31/8/18 6:11	57	1/9/18 23:16 60	3/9/18 0:21 53	4/9/18 1:26 61		6/9/18 3:36 58
31/8/18 6:16	58	1/9/18 23:21 60	3/9/18 0:26 54	4/9/18 1:31 61	5/9/18 2:36 55	6/9/18 3:41 57
31/8/18 6:21	56	1/9/18 23:26 60	3/9/18 0:31 52	4/9/18 1:36 53	5/9/18 2:41 55	6/9/18 3:46 57
31/8/18 6:26	58	1/9/18 23:31 61	3/9/18 0:36 54	4/9/18 1:41 61	5/9/18 2:46 55	6/9/18 3:51 57
31/8/18 6:31	59	1/9/18 23:36 60	3/9/18 0:41 54	4/9/18 1:46 60	5/9/18 2:51 55	6/9/18 3:56 57
31/8/18 6:36	60	1/9/18 23:41 61	3/9/18 0:46 49	4/9/18 1:51 61	5/9/18 2:56 55	6/9/18 4:01 57
31/8/18 6:41	59	1/9/18 23:46 61	3/9/18 0:51 51	4/9/18 1:56 44	5/9/18 3:01 56	6/9/18 4:06 57
31/8/18 6:46	59	1/9/18 23:51 61	3/9/18 0:56 49	4/9/18 2:01 61	5/9/18 3:06 55	6/9/18 4:11 56
31/8/18 6:51	58	1/9/18 23:56 60	3/9/18 1:01 47	4/9/18 2:06 61	5/9/18 3:11 55	6/9/18 4:16 57
31/8/18 6:56	60	2/9/18 0:01 60	3/9/18 1:06 51	4/9/18 2:11 61	5/9/18 3:16 55	6/9/18 4:21 57
31/8/18 23:01	61	2/9/18 0:06 59	3/9/18 1:11 45	4/9/18 2:16 61	5/9/18 3:21 56	6/9/18 4:26 57
31/8/18 23:06	60	2/9/18 0:11 60	3/9/18 1:16 61	4/9/18 2:21 61	5/9/18 3:26 55	6/9/18 4:31 57
31/8/18 23:11	60	2/9/18 0:16 60	3/9/18 1:21 57	4/9/18 2:26 60	5/9/18 3:31 55	6/9/18 4:36 57
31/8/18 23:16	60	2/9/18 0:21 60	3/9/18 1:26 49	4/9/18 2:31 61	5/9/18 3:36 56	6/9/18 4:41 56
31/8/18 23:21	60	2/9/18 0:26 60	3/9/18 1:31 51	4/9/18 2:36 61	5/9/18 3:41 55	6/9/18 4:46 57
31/8/18 23:26	60	2/9/18 0:31 60	3/9/18 1:36 61	4/9/18 2:41 61	5/9/18 3:46 56	6/9/18 4:51 57
31/8/18 23:31	60	2/9/18 0:36 60	3/9/18 1:41 61	4/9/18 2:46 61	5/9/18 3:51 54	6/9/18 4:56 57
31/8/18 23:36	60	2/9/18 0:41 60	3/9/18 1:46 45	4/9/18 2:51 60	5/9/18 3:56 55	6/9/18 5:01 57
31/8/18 23:41	60	2/9/18 0:46 60	3/9/18 1:51 41	4/9/18 2:56 61	5/9/18 4:01 55	6/9/18 5:06 57
31/8/18 23:46	59	2/9/18 0:51 60	3/9/18 1:56 61	4/9/18 3:01 61	5/9/18 4:06 56	6/9/18 5:11 57
31/8/18 23:51	60	2/9/18 0:56 59	3/9/18 2:01 61	4/9/18 3:06 41	5/9/18 4:11 55	6/9/18 5:16 57
31/8/18 23:56	59	2/9/18 1:01 59	3/9/18 2:06 61	4/9/18 3:11 61	5/9/18 4:16 54	6/9/18 5:21 57
1/9/18 0:01	60	2/9/18 1:06 59	3/9/18 2:11 45	4/9/18 3:16 61	5/9/18 4:21 55	6/9/18 5:26 58
1/9/18 0:06	59	2/9/18 1:11 59	3/9/18 2:16 42	4/9/18 3:21 61	5/9/18 4:26 56	6/9/18 5:31 58
1/9/18 0:11	59	2/9/18 1:16 59	3/9/18 2:21 61	4/9/18 3:26 60	5/9/18 4:31 54	6/9/18 5:36 57
1/9/18 0:16	60	2/9/18 1:21 59	3/9/18 2:26 52	4/9/18 3:31 61	5/9/18 4:36 55	6/9/18 5:41 57
1/9/18 0:21	60	2/9/18 1:26 59	3/9/18 2:31 43	4/9/18 3:36 60	5/9/18 4:41 55	6/9/18 5:46 58
1/9/18 0:26	59	2/9/18 1:31 59	3/9/18 2:36 39	4/9/18 3:41 48	5/9/18 4:46 55	6/9/18 5:51 58
1/9/18 0:31	59	2/9/18 1:36 58	3/9/18 2:41 61	4/9/18 3:46 61	5/9/18 4:51 55	6/9/18 5:56 58
1/9/18 0:36	59	2/9/18 1:41 59	3/9/18 2:46 57	4/9/18 3:51 61	5/9/18 4:56 55	6/9/18 6:01 58
1/9/18 0:41	59	2/9/18 1:46 58	3/9/18 2:51 46	4/9/18 3:56 46	5/9/18 5:01 55	6/9/18 6:06 59
1/9/18 0:46	59	2/9/18 1:51 60	3/9/18 2:56 61	4/9/18 4:01 61	5/9/18 5:06 56	6/9/18 6:11 60
1/9/18 0:51		2/9/18 1:56 58	3/9/18 3:01 61	4/9/18 4:06 61	5/9/18 5:11 56	6/9/18 6:16 59
1/9/18 0:56	59 59	2/9/18 2:01 58	3/9/18 3:06 61	4/9/18 4:11 47	5/9/18 5:16 55	6/9/18 6:21 60
1/9/18 1:01	59	2/9/18 2:06 57	3/9/18 3:11 61	4/9/18 4:16 61	5/9/18 5:21 56	6/9/18 6:26 59
1/9/18 1:06	59	2/9/18 2:11 58	3/9/18 3:16 61	4/9/18 4:21 61	5/9/18 5:26 57	6/9/18 6:31 61
1/9/18 1:11	59	2/9/18 2:16 58	3/9/18 3:21 61	4/9/18 4:26 49	5/9/18 5:31 57	6/9/18 6:36 47
1/9/18 1:16	59	2/9/18 2:21 57	3/9/18 3:26 61	4/9/18 4:31 44	5/9/18 5:36 56	6/9/18 6:41 61
1/9/18 1:21	59	2/9/18 2:26 58	3/9/18 3:31 49	4/9/18 4:36 43	5/9/18 5:41 57	6/9/18 6:46 42
1/9/18 1:26	58	2/9/18 2:31 57	3/9/18 3:36 42	4/9/18 4:41 61	5/9/18 5:46 58	6/9/18 6:51 60
1/9/18 1:31	58	2/9/18 2:36 57	3/9/18 3:41 61	4/9/18 4:46 61	5/9/18 5:51 57	6/9/18 6:56 46
1/9/18 1:36	58	2/9/18 2:41 57	3/9/18 3:46 51	4/9/18 4:51 45	5/9/18 5:56 57	6/9/18 23:01 60
1/9/18 1:41	59	2/9/18 2:46 57	3/9/18 3:51 61	4/9/18 4:56 61	5/9/18 6:01 58	6/9/18 23:06 61
1/9/18 1:46	59	2/9/18 2:51 56	3/9/18 3:56 61	4/9/18 5:01 61	5/9/18 6:06 58	6/9/18 23:11 60
1/9/18 1:51	58	2/9/18 2:56 57	3/9/18 4:01 61	4/9/18 5:06 61	5/9/18 6:11 58	6/9/18 23:16 60
1/9/18 1:56	59	2/9/18 3:01 57	3/9/18 4:06 61	4/9/18 5:11 61	5/9/18 6:16 59	6/9/18 23:21 60
1/9/18 2:01	58	2/9/18 3:06 56	3/9/18 4:11 61	4/9/18 5:16 47	5/9/18 6:21 60	6/9/18 23:26 60
1/9/18 2:06	58	2/9/18 3:11 57	3/9/18 4:16 49	4/9/18 5:21 61	5/9/18 6:26 60	6/9/18 23:31 60
1/9/18 2:11	59	2/9/18 3:16 57	3/9/18 4:21 49	4/9/18 5:26 44	5/9/18 6:31 60	6/9/18 23:36 60
1/9/18 2:16	58	2/9/18 3:21 57	3/9/18 4:26 48	4/9/18 5:31 50	5/9/18 6:36 60	6/9/18 23:41 59
1/9/18 2:21	58	2/9/18 3:26 57	3/9/18 4:31 51	4/9/18 5:36 52	5/9/18 6:41 43	6/9/18 23:46 60
1/9/18 2:26	57	2/9/18 3:31 57	3/9/18 4:36 52	4/9/18 5:41 50	5/9/18 6:46 49	6/9/18 23:51 59
1/9/18 2:31	57	2/9/18 3:36 57	3/9/18 4:41 50	4/9/18 5:46 56	5/9/18 6:51 61	6/9/18 23:56 59
1/9/18 2:36	57	2/9/18 3:41 57	3/9/18 4:46 50	4/9/18 5:51 54	5/9/18 6:56 61	7/9/18 0:01 60
1/9/18 2:41	57	2/9/18 3:46 57	3/9/18 4:51 53	4/9/18 5:56 54	5/9/18 23:01 60	7/9/18 0:06 60
1/9/18 2:46	57	2/9/18 3:51 57	3/9/18 4:56 53	4/9/18 6:01 56	5/9/18 23:06 60	7/9/18 0:11 59
1/9/18 2:51	57	2/9/18 3:56 57	3/9/18 5:01 51	4/9/18 6:06 57	5/9/18 23:11 61 5/0/18 23:16 60	7/9/18 0:16 59
1/9/18 2:56	58	2/9/18 4:01 57	3/9/18 5:06 54	4/9/18 6:11 56	5/9/18 23:16 60	7/9/18 0:21 59
1/9/18 3:01	57	2/9/18 4:06 57	3/9/18 5:11 53	4/9/18 6:16 56	5/9/18 23:21 60	7/9/18 0:26 59
1/9/18 3:06	58 57	2/9/18 4:11 60 2/9/18 4:16 56	3/9/18 5:16 55 3/9/18 5:21 54	4/9/18 6:21 57	5/9/18 23:26 61	7/9/18 0:31 59 7/9/18 0:36 59
1/9/18 3:11 1/9/18 3:16	57	2/9/18 4:16 56 2/9/18 4:21 56	3/9/18 5:26 54	4/9/18 6:26 57 4/9/18 6:31 58	5/9/18 23:31 60 5/9/18 23:36 60	7/9/18 0:41 58
1/9/18 3:21	57	2/9/18 4:26 58	3/9/18 5:31 54	4/9/18 6:36 59	5/9/18 23:41 59	7/9/18 0:46 58
1/9/18 3:26	56	2/9/18 4:31 57	3/9/18 5:36 54	4/9/18 6:41 59	5/9/18 23:46 59	7/9/18 0:51 58
1/9/18 3:31	57	2/9/18 4:36 57	3/9/18 5:41 55	4/9/18 6:46 59	5/9/18 23:51 60	7/9/18 0:56 58
1/9/18 3:36	57	2/9/18 4:41 58	3/9/18 5:46 56	4/9/18 6:51 59	5/9/18 23:56 59	7/9/18 1:01 58
1/9/18 3:41	57	2/9/18 4:46 57	3/9/18 5:51 55	4/9/18 6:56 59	6/9/18 0:01 59	7/9/18 1:06 58
1/9/18 3:46	57	2/9/18 4:51 57	3/9/18 5:56 56	4/9/18 23:01 60	6/9/18 0:06 60	7/9/18 1:11 58
1/9/18 3:51	56	2/9/18 4:56 57	3/9/18 6:01 56	4/9/18 23:06 60	6/9/18 0:11 59	7/9/18 1:16 58
1/9/18 3:56	56	2/9/18 5:01 57	3/9/18 6:06 57	4/9/18 23:11 60	6/9/18 0:16 59	7/9/18 1:21 58
1/9/18 4:01	56	2/9/18 5:06 57	3/9/18 6:11 58	4/9/18 23:16 59	6/9/18 0:21 59	7/9/18 1:26 58
1/9/18 4:06	57	2/9/18 5:11 57	3/9/18 6:16 59	4/9/18 23:21 59	6/9/18 0:26 59	7/9/18 1:31 58
1/9/18 4:11	56	2/9/18 5:16 57	3/9/18 6:21 59	4/9/18 23:26 60	6/9/18 0:31 59	7/9/18 1:36 58
1/9/18 4:16	56	2/9/18 5:21 57	3/9/18 6:26 58	4/9/18 23:31 60	6/9/18 0:36 58	7/9/18 1:41 58
1/9/18 4:21	56	2/9/18 5:26 57	3/9/18 6:31 60	4/9/18 23:36 59	6/9/18 0:41 59	7/9/18 1:46 57
1/9/18 4:26	56	2/9/18 5:31 57	3/9/18 6:36 59	4/9/18 23:41 59	6/9/18 0:46 58	7/9/18 1:51 58
1/9/18 4:31	57	2/9/18 5:36 56	3/9/18 6:41 60	4/9/18 23:46 59	6/9/18 0:51 59	7/9/18 1:56 56
1/9/18 4:36	56	2/9/18 5:41 56	3/9/18 6:46 60	4/9/18 23:51 58		7/9/18 2:01 56
1, 0/ 10 4.00	56 56	2/9/18 5:41 56 2/9/18 5:46 56	3/9/18 6:46 60	4/9/18 23:51 58	6/9/18 0:56 59 6/9/18 1:01 58	7/9/18 2:01 56


e <u>al-time Nois</u> 9/18 2:11 9/18 2:16	57 56	RTN4 (Causeway Bay Co 8/9/18 3:16 57 8/9/18 3:21 56	9/9/18 4:21 9/9/18 4:26	56 55	10/9/18 5:26 57 10/9/18 5:31 57	11/9/18 6:31 60 11/9/18 6:36 44	12/9/18 23:36 12/9/18 23:41
9/18 2:21 9/18 2:26	58 56	8/9/18 3:26 56 8/9/18 3:31 56	9/9/18 4:31 9/9/18 4:36	55 56	10/9/18 5:36 57 10/9/18 5:41 57	11/9/18 6:41 50 11/9/18 6:46 49	12/9/18 23:46 12/9/18 23:51
9/18 2:31	56	8/9/18 3:36 56	9/9/18 4:41	56	10/9/18 5:46 58	11/9/18 6:51 51	12/9/18 23:56
9/18 2:36	57	8/9/18 3:41 55	9/9/18 4:46	55	10/9/18 5:51 57	11/9/18 6:56 49	13/9/18 0:01
9/18 2:41 9/18 2:46	57 56	8/9/18 3:46 57 8/9/18 3:51 56	9/9/18 4:51 9/9/18 4:56	56 57	10/9/18 5:56 58 10/9/18 6:01 57	11/9/18 23:01 60 11/9/18 23:06 59	13/9/18 0:06 13/9/18 0:11
9/18 2:51	57	8/9/18 3:56 56	9/9/18 5:01	55	10/9/18 6:06 58	11/9/18 23:11 60	13/9/18 0:16
9/18 2:56	57	8/9/18 4:01 55	9/9/18 5:06	56	10/9/18 6:11 59	11/9/18 23:16 60	13/9/18 0:21
9/18 3:01 9/18 3:06	55 56	8/9/18 4:06 55 8/9/18 4:11 55	9/9/18 5:11 9/9/18 5:16	56 56	10/9/18 6:16 59 10/9/18 6:21 60	11/9/18 23:21 59 11/9/18 23:26 59	13/9/18 0:26 13/9/18 0:31
9/18 3:11	56	8/9/18 4:16 53	9/9/18 5:21	56	10/9/18 6:26 60	11/9/18 23:31 58	13/9/18 0:36
9/18 3:16 9/18 3:21	57 56	8/9/18 4:21 56 8/9/18 4:26 55	9/9/18 5:26 9/9/18 5:31	56 56	10/9/18 6:31 60 10/9/18 6:36 60	11/9/18 23:36 58 11/9/18 23:41 60	13/9/18 0:41 13/9/18 0:46
9/18 3:26	56	8/9/18 4:31 56	9/9/18 5:36	56	10/9/18 6:41 61	11/9/18 23:46 59	13/9/18 0:51
9/18 3:31	55	8/9/18 4:36 56	9/9/18 5:41	56	10/9/18 6:46 50	11/9/18 23:51 58	13/9/18 0:56
9/18 3:36 9/18 3:41	56 56	8/9/18 4:41 55 8/9/18 4:46 55	9/9/18 5:46 9/9/18 5:51	57 57	10/9/18 6:51 61 10/9/18 6:56 60	11/9/18 23:56 60 12/9/18 0:01 58	13/9/18 1:01 13/9/18 1:06
9/18 3:46	58	8/9/18 4:51 56	9/9/18 5:56	56	10/9/18 23:01 47	12/9/18 0:06 59	13/9/18 1:11
9/18 3:51	57	8/9/18 4:56 55	9/9/18 6:01	57	10/9/18 23:06 59	12/9/18 0:11 58	13/9/18 1:16
9/18 3:56 9/18 4:01	39 56	8/9/18 5:01 55 8/9/18 5:06 55	9/9/18 6:06 9/9/18 6:11	57 57	10/9/18 23:11 60 10/9/18 23:16 60	12/9/18 0:16 58 12/9/18 0:21 58	13/9/18 1:21 13/9/18 1:26
9/18 4:06	56	8/9/18 5:11 55	9/9/18 6:16	57	10/9/18 23:21 59	12/9/18 0:26 47	13/9/18 1:31
9/18 4:11 9/18 4:16	56 56	8/9/18 5:16 55 8/9/18 5:21 55	9/9/18 6:21 9/9/18 6:26	60 59	10/9/18 23:26 43 10/9/18 23:31 58	12/9/18 0:31 60 12/9/18 0:36 57	13/9/18 1:36 13/9/18 1:41
/18 4:21	56	8/9/18 5:26 56	9/9/18 6:31	58	10/9/18 23:36 58	12/9/18 0:41 58	13/9/18 1:46
/18 4:26	56	8/9/18 5:31 55	9/9/18 6:36	59	10/9/18 23:41 59	12/9/18 0:46 53	13/9/18 1:51
9/18 4:31 9/18 4:36	55 56	8/9/18 5:36 56 8/9/18 5:41 56	9/9/18 6:41 9/9/18 6:46	58 59	10/9/18 23:46 59 10/9/18 23:51 58	12/9/18 0:51 57 12/9/18 0:56 58	13/9/18 1:56 13/9/18 2:01
/18 4:41	57	8/9/18 5:46 56	9/9/18 6:51	58	10/9/18 23:56 59	12/9/18 1:01 57	13/9/18 2:06
9/18 4:46	55	8/9/18 5:51 57	9/9/18 6:56	58	11/9/18 0:01 59	12/9/18 1:06 57	13/9/18 2:11
9/18 4:51 9/18 4:56	57 57	8/9/18 5:56 57 8/9/18 6:01 57	9/9/18 23:01 9/9/18 23:06	60 60	11/9/18 0:06 39 11/9/18 0:11 53	12/9/18 1:11 57 12/9/18 1:16 57	13/9/18 2:16 13/9/18 2:21
/18 5:01	56	8/9/18 6:06 57	9/9/18 23:11	60	11/9/18 0:16 61	12/9/18 1:21 56	13/9/18 2:26
/18 5:06 /18 5:11	57 57	8/9/18 6:11 58	9/9/18 23:16	60 53	11/9/18 0:21 59	12/9/18 1:26 57 12/9/18 1:31 57	13/9/18 2:31
/18 5:11 /18 5:16	57 57	8/9/18 6:16 57 8/9/18 6:21 58	9/9/18 23:21 9/9/18 23:26	53 58	11/9/18 0:26 58 11/9/18 0:31 58	12/9/18 1:31 57	13/9/18 2:36 13/9/18 2:41
18 5:21	57	8/9/18 6:26 59	9/9/18 23:31	51	11/9/18 0:36 58	12/9/18 1:41 57	13/9/18 2:46
/18 5:26 /18 5:31	58 57	8/9/18 6:31 59 8/9/18 6:36 59	9/9/18 23:36 9/9/18 23:41	45 60	11/9/18 0:41 58 11/9/18 0:46 57	12/9/18 1:46 57 12/9/18 1:51 56	13/9/18 2:51 13/9/18 2:56
18 5:36	57	8/9/18 6:41 59	9/9/18 23:46	43	11/9/18 0:51 58	12/9/18 1:56 55	13/9/18 3:01
18 5:41	58	8/9/18 6:46 60	9/9/18 23:51	57	11/9/18 0:56 59	12/9/18 2:01 56	13/9/18 3:06
'18 5:46 '18 5:51	57 58	8/9/18 6:51 60 8/9/18 6:56 60	9/9/18 23:56 10/9/18 0:01	60 60	11/9/18 1:01 57 11/9/18 1:06 58	12/9/18 2:06 56 12/9/18 2:11 54	13/9/18 3:11 13/9/18 3:16
18 5:56	58	8/9/18 23:01 60	10/9/18 0:06	60	11/9/18 1:11 58	12/9/18 2:16 57	13/9/18 3:21
18 6:01 18 6:06	58 59	8/9/18 23:06 59 8/9/18 23:11 60	10/9/18 0:11 10/9/18 0:16	58 59	11/9/18 1:16 57 11/9/18 1:21 60	12/9/18 2:21 56 12/9/18 2:26 55	13/9/18 3:26
18 6:11	59	8/9/18 23:16 59	10/9/18 0:21	58	11/9/18 1:21 60 11/9/18 1:26 58	12/9/18 2:31 56	13/9/18 3:31 13/9/18 3:36
18 6:16	59	8/9/18 23:21 59	10/9/18 0:26	58	11/9/18 1:31 59	12/9/18 2:36 55	13/9/18 3:41
18 6:21 18 6:26	59 60	8/9/18 23:26 59 8/9/18 23:31 59	10/9/18 0:31 10/9/18 0:36	57 57	11/9/18 1:36 56 11/9/18 1:41 56	12/9/18 2:41 57 12/9/18 2:46 56	13/9/18 3:46 13/9/18 3:51
18 6:31	60	8/9/18 23:36 59	10/9/18 0:41	57	11/9/18 1:46 58	12/9/18 2:51 57	13/9/18 3:56
18 6:36	60	8/9/18 23:41 58	10/9/18 0:46	57	11/9/18 1:51 56	12/9/18 2:56 55	13/9/18 4:01
'18 6:41 '18 6:46	51 43	8/9/18 23:46 59 8/9/18 23:51 59	10/9/18 0:51 10/9/18 0:56	56 60	11/9/18 1:56 60 11/9/18 2:01 57	12/9/18 3:01 55 12/9/18 3:06 54	13/9/18 4:06 13/9/18 4:11
/18 6:51	61	8/9/18 23:56 59	10/9/18 1:01	57	11/9/18 2:06 56	12/9/18 3:11 55	13/9/18 4:16
/18 6:56 /18 23:01	46 60	9/9/18 0:01 58 9/9/18 0:06 59	10/9/18 1:06 10/9/18 1:11	57 57	11/9/18 2:11 56 11/9/18 2:16 56	12/9/18 3:16 55 12/9/18 3:21 55	13/9/18 4:21 13/9/18 4:26
/18 23:06	60	9/9/18 0:11 59	10/9/18 1:16	56	11/9/18 2:21 55	12/9/18 3:26 56	13/9/18 4:31
18 23:11	60	9/9/18 0:16 58	10/9/18 1:21	56	11/9/18 2:26 55	12/9/18 3:31 55	13/9/18 4:36
/18 23:16 /18 23:21	60 59	9/9/18 0:21 59 9/9/18 0:26 59	10/9/18 1:26 10/9/18 1:31	57 56	11/9/18 2:31 57 11/9/18 2:36 55	12/9/18 3:36 55 12/9/18 3:41 55	13/9/18 4:41 13/9/18 4:46
18 23:26	61	9/9/18 0:31 58	10/9/18 1:36	56	11/9/18 2:41 56	12/9/18 3:46 55	13/9/18 4:51
18 23:31 18 23:36	59	9/9/18 0:36 58	10/9/18 1:41 10/9/18 1:46	56	11/9/18 2:46 55	12/9/18 3:51 56	13/9/18 4:56 13/9/18 5:01
18 23:36	59 58	9/9/18 0:41 58 9/9/18 0:46 59	10/9/18 1:46	55 56	11/9/18 2:51 57 11/9/18 2:56 56	12/9/18 3:56 54 12/9/18 4:01 55	13/9/18 5:01
18 23:46	59	9/9/18 0:51 58	10/9/18 1:56	56	11/9/18 3:01 55	12/9/18 4:06 54	13/9/18 5:11
18 23:51 18 23:56	59 58	9/9/18 0:56 58 9/9/18 1:01 58	10/9/18 2:01 10/9/18 2:06	55 55	11/9/18 3:06 56 11/9/18 3:11 56	12/9/18 4:11 55 12/9/18 4:16 55	13/9/18 5:16 13/9/18 5:21
18 0:01	58	9/9/18 1:06 58	10/9/18 2:11	55	11/9/18 3:16 56	12/9/18 4:21 55	13/9/18 5:26
18 0:06	59	9/9/18 1:11 58	10/9/18 2:16	55	11/9/18 3:21 54	12/9/18 4:26 55	13/9/18 5:31
18 0:11 18 0:16	59 59	9/9/18 1:16 58 9/9/18 1:21 58	10/9/18 2:21 10/9/18 2:26	56 54	11/9/18 3:26 55 11/9/18 3:31 57	12/9/18 4:31 55 12/9/18 4:36 56	13/9/18 5:36 13/9/18 5:41
18 0:21	58	9/9/18 1:26 57	10/9/18 2:31	55	11/9/18 3:36 57	12/9/18 4:41 55	13/9/18 5:46
18 0:26	58	9/9/18 1:31 57	10/9/18 2:36	55	11/9/18 3:41 55	12/9/18 4:46 55	13/9/18 5:51
18 0:31 18 0:36	58 59	9/9/18 1:36 58 9/9/18 1:41 58	10/9/18 2:41 10/9/18 2:46	55 56	11/9/18 3:46 55 11/9/18 3:51 55	12/9/18 4:51 55 12/9/18 4:56 55	13/9/18 5:56 13/9/18 6:01
18 0:41	58	9/9/18 1:46 56	10/9/18 2:51	56	11/9/18 3:56 55	12/9/18 5:01 55	13/9/18 6:06
18 0:46	58	9/9/18 1:51 57	10/9/18 2:56	54	11/9/18 4:01 55	12/9/18 5:06 56	13/9/18 6:11
18 0:51 18 0:56	58 58	9/9/18 1:56 57 9/9/18 2:01 57	10/9/18 3:01 10/9/18 3:06	54 54	11/9/18 4:06 55 11/9/18 4:11 55	12/9/18 5:11 55 12/9/18 5:16 55	13/9/18 6:16 13/9/18 6:21
8 1:01	58	9/9/18 2:06 56	10/9/18 3:11	54	11/9/18 4:16 55	12/9/18 5:21 55	13/9/18 6:26
8 1:06	57	9/9/18 2:11 56	10/9/18 3:16	55	11/9/18 4:21 55	12/9/18 5:26 57	13/9/18 6:31
18 1:11 18 1:16	58 56	9/9/18 2:16 56 9/9/18 2:21 57	10/9/18 3:21 10/9/18 3:26	55 55	11/9/18 4:26 56 11/9/18 4:31 55	12/9/18 5:31 56 12/9/18 5:36 56	13/9/18 6:36 13/9/18 6:41
18 1:21	57	9/9/18 2:26 57	10/9/18 3:31	55	11/9/18 4:36 56	12/9/18 5:41 57	13/9/18 6:46
18 1:26	57 56	9/9/18 2:31 57	10/9/18 3:36	55	11/9/18 4:41 57	12/9/18 5:46 56	13/9/18 6:51
18 1:31 18 1:36	56 57	9/9/18 2:36 57 9/9/18 2:41 57	10/9/18 3:41 10/9/18 3:46	55 55	11/9/18 4:46 55 11/9/18 4:51 55	12/9/18 5:51 58 12/9/18 5:56 57	13/9/18 6:56 13/9/18 23:01
18 1:41	56	9/9/18 2:46 57	10/9/18 3:51	54	11/9/18 4:56 57	12/9/18 6:01 57	13/9/18 23:06
18 1:46 18 1:51	56 58	9/9/18 2:51 57 9/9/18 2:56 57	10/9/18 3:56 10/9/18 4:01	54 56	11/9/18 5:01 55 11/9/18 5:06 56	12/9/18 6:06 58 12/9/18 6:11 58	13/9/18 23:11 13/9/18 23:16
18 1:56	57	9/9/18 3:01 57	10/9/18 4:01	56	11/9/18 5:11 56	12/9/18 6:16 58	13/9/18 23:21
18 2:01	58	9/9/18 3:06 56	10/9/18 4:11	55	11/9/18 5:16 56	12/9/18 6:21 59	13/9/18 23:26
18 2:06 18 2:11	56 57	9/9/18 3:11 57 9/9/18 3:16 57	10/9/18 4:16 10/9/18 4:21	55 55	11/9/18 5:21 56 11/9/18 5:26 58	12/9/18 6:26 60 12/9/18 6:31 60	13/9/18 23:31 13/9/18 23:36
18 2:16	57	9/9/18 3:16 57	10/9/18 4:21	55 56	11/9/18 5:26 58	12/9/18 6:36 60	13/9/18 23:36
18 2:21	57	9/9/18 3:26 57	10/9/18 4:31	55	11/9/18 5:36 57	12/9/18 6:41 60	13/9/18 23:46
18 2:26 18 2:31	57 59	9/9/18 3:31 56 9/9/18 3:36 56	10/9/18 4:36 10/9/18 4:41	56 56	11/9/18 5:41 58 11/9/18 5:46 58	12/9/18 6:46 60 12/9/18 6:51 60	13/9/18 23:51 13/9/18 23:56
18 2:31	59 58	9/9/18 3:36 56 9/9/18 3:41 56	10/9/18 4:41	56 55	11/9/18 5:51 57	12/9/18 6:51 60	14/9/18 0:01
18 2:41	57	9/9/18 3:46 58	10/9/18 4:51	55	11/9/18 5:56 58	12/9/18 23:01 59	14/9/18 0:06
18 2:46 18 2:51	58 58	9/9/18 3:51 56 9/9/18 3:56 56	10/9/18 4:56 10/9/18 5:01	55 55	11/9/18 6:01 58 11/9/18 6:06 59	12/9/18 23:06 59 12/9/18 23:11 59	14/9/18 0:11 14/9/18 0:16
18 2:51	58 57	9/9/18 3:56 56 9/9/18 4:01 56	10/9/18 5:01	55 56	11/9/18 6:11 59	12/9/18 23:11 59	14/9/18 0:16
18 3:01 18 3:06	55	9/9/18 4:06 55	10/9/18 5:11	57	11/9/18 6:16 59	12/9/18 23:21 59	14/9/18 0:26
	56	9/9/18 4:11 55	10/9/18 5:16 10/9/18 5:21	55	11/9/18 6:21 59	12/9/18 23:26 59 12/9/18 23:31 59	14/9/18 0:31

14/9/18 0:41 14/9/18 0:46	<u>e Data</u> 58 55	RTN4 (Causeway Bay Commun 15/9/18 1:46 54 15/9/18 1:51 56	16/9/18 2:51 49 16/9/18 2:56 60	17/9/18 3:56 59 17/9/18 4:01 57	18/9/18 5:01 56 18/9/18 5:06 57	19/9/18 6:06 59 19/9/18 6:11 58
14/9/18 0:51	56	15/9/18 1:56 54	16/9/18 3:01 59	17/9/18 4:06 55	18/9/18 5:11 56	19/9/18 6:16 59
14/9/18 0:56	55	15/9/18 2:01 60	16/9/18 3:06 58	17/9/18 4:11 56	18/9/18 5:16 57	19/9/18 6:21 59
14/9/18 1:01	55	15/9/18 2:06 58	16/9/18 3:11 60	17/9/18 4:16 54	18/9/18 5:21 57	19/9/18 6:26 59
14/9/18 1:06	56	15/9/18 2:11 58	16/9/18 3:16 59	17/9/18 4:21 54	18/9/18 5:26 57	19/9/18 6:31 60
14/9/18 1:11	56	15/9/18 2:16 59	16/9/18 3:21 60	17/9/18 4:26 55	18/9/18 5:31 57	19/9/18 6:36 60
14/9/18 1:16	55	15/9/18 2:21 59	16/9/18 3:26 60	17/9/18 4:31 55	18/9/18 5:36 57	19/9/18 6:41 48
14/9/18 1:21	55	15/9/18 2:26 60	16/9/18 3:31 57	17/9/18 4:36 55	18/9/18 5:41 58	19/9/18 6:46 61
14/9/18 1:26	53	15/9/18 2:31 60	16/9/18 3:36 61	17/9/18 4:41 54	18/9/18 5:46 57	19/9/18 6:51 60
14/9/18 1:31	54	15/9/18 2:36 55	16/9/18 3:41 55	17/9/18 4:46 55	18/9/18 5:51 57	19/9/18 6:56 60
14/9/18 1:36	54	15/9/18 2:41 60	16/9/18 3:46 60	17/9/18 4:51 54	18/9/18 5:56 59	19/9/18 23:01 60
14/9/18 1:41	55	15/9/18 2:46 60	16/9/18 3:51 60	17/9/18 4:56 55	18/9/18 6:01 57	19/9/18 23:06 59
14/9/18 1:46	54	15/9/18 2:51 60	16/9/18 3:56 55	17/9/18 5:01 55	18/9/18 6:06 59	19/9/18 23:11 60
14/9/18 1:51	54	15/9/18 2:56 59	16/9/18 4:01 48	17/9/18 5:06 54	18/9/18 6:11 58	19/9/18 23:16 60
14/9/18 1:56	54	15/9/18 3:01 59	16/9/18 4:06 42	17/9/18 5:11 54	18/9/18 6:16 58	19/9/18 23:21 59
14/9/18 2:01	54	15/9/18 3:06 59	16/9/18 4:11 58	17/9/18 5:16 55	18/9/18 6:21 59	19/9/18 23:26 59
14/9/18 2:06	53	15/9/18 3:11 59	16/9/18 4:16 58	17/9/18 5:21 55	18/9/18 6:26 60	19/9/18 23:31 60
14/9/18 2:11	54	15/9/18 3:16 59	16/9/18 4:21 59	17/9/18 5:26 55	18/9/18 6:31 60	19/9/18 23:36 59
14/9/18 2:16	55	15/9/18 3:21 45	16/9/18 4:26 61	17/9/18 5:31 55	18/9/18 6:36 60	19/9/18 23:41 59
14/9/18 2:21	53	15/9/18 3:26 52	16/9/18 4:31 61	17/9/18 5:36 55	18/9/18 6:41 60	19/9/18 23:46 59
14/9/18 2:26	51	15/9/18 3:31 56	16/9/18 4:36 60	17/9/18 5:41 55	18/9/18 6:46 61	19/9/18 23:51 60
14/9/18 2:31	50 54	15/9/18 3:36 59	16/9/18 4:41 60	17/9/18 5:46 56	18/9/18 6:51 60	19/9/18 23:56 59
14/9/18 2:36	54	15/9/18 3:41 59	16/9/18 4:46 60	17/9/18 5:51 56	18/9/18 6:56 60	20/9/18 0:01 59
14/9/18 2:41		15/9/18 3:46 60	16/9/18 4:51 60	17/9/18 5:56 57	18/9/18 23:01 59	20/9/18 0:06 59
14/9/18 2:46	53	15/9/18 3:51 60	16/9/18 4:56 61	17/9/18 6:01 56	18/9/18 23:06 60	20/9/18 0:11 58
14/9/18 2:51	54	15/9/18 3:56 59	16/9/18 5:01 49	17/9/18 6:06 57	18/9/18 23:11 59	20/9/18 0:16 59
14/9/18 2:56	52	15/9/18 4:01 60	16/9/18 5:06 59	17/9/18 6:11 58	18/9/18 23:16 59	20/9/18 0:21 59
14/9/18 3:01	54	15/9/18 4:06 52	16/9/18 5:11 53	17/9/18 6:16 57	18/9/18 23:21 59	20/9/18 0:26 59
14/9/18 3:06	53	15/9/18 4:11 49	16/9/18 5:16 60	17/9/18 6:21 58	18/9/18 23:26 59	20/9/18 0:31 58
14/9/18 3:11	53	15/9/18 4:16 50	16/9/18 5:21 60	17/9/18 6:26 57	18/9/18 23:31 59	20/9/18 0:36 59
14/9/18 3:16	54	15/9/18 4:21 59	16/9/18 5:26 58	17/9/18 6:31 58	18/9/18 23:36 58	20/9/18 0:41 57
14/9/18 3:21	53	15/9/18 4:26 51	16/9/18 5:31 39	17/9/18 6:36 58	18/9/18 23:41 59	20/9/18 0:46 58
14/9/18 3:26	53	15/9/18 4:31 52	16/9/18 5:36 47	17/9/18 6:41 58	18/9/18 23:46 58	20/9/18 0:51 57
14/9/18 3:31	54	15/9/18 4:36 46	16/9/18 5:41 59	17/9/18 6:46 58	18/9/18 23:51 58	20/9/18 0:56 58
14/9/18 3:36	53	15/9/18 4:41 55	16/9/18 5:46 52	17/9/18 6:51 59	18/9/18 23:56 58	20/9/18 1:01 58
14/9/18 3:41	53	15/9/18 4:46 57	16/9/18 5:51 60	17/9/18 6:56 59	19/9/18 0:01 57	20/9/18 1:06 57
14/9/18 3:46	53	15/9/18 4:51 61	16/9/18 5:56 41	17/9/18 23:01 59	19/9/18 0:06 57	20/9/18 1:11 57
14/9/18 3:46	53 51	15/9/18 4:56 56	16/9/18 6:01 61	17/9/18 23:06 60	19/9/18 0:11 57	20/9/18 1:16 57
14/9/18 3:56	51	15/9/18 5:01 50	16/9/18 6:06 55	17/9/18 23:11 59	19/9/18 0:16 58	20/9/18 1:21 57
14/9/18 4:01	53	15/9/18 5:06 51	16/9/18 6:11 53	17/9/18 23:16 59	19/9/18 0:21 58	20/9/18 1:26 57
14/9/18 4:06	52	15/9/18 5:11 53	16/9/18 6:16 60	17/9/18 23:21 60	19/9/18 0:26 57	20/9/18 1:31 57
14/9/18 4:11	54	15/9/18 5:16 51	16/9/18 6:21 62	17/9/18 23:26 59	19/9/18 0:31 58	20/9/18 1:36 56
14/9/18 4:16	51	15/9/18 5:21 54	16/9/18 6:26 59	17/9/18 23:31 59	19/9/18 0:36 57	20/9/18 1:41 56
14/9/18 4:21	52	15/9/18 5:26 56	16/9/18 6:31 56	17/9/18 23:36 58	19/9/18 0:41 57	20/9/18 1:46 57
14/9/18 4:26	55	15/9/18 5:31 59	16/9/18 6:36 58	17/9/18 23:41 58	19/9/18 0:46 57	20/9/18 1:51 57
14/9/18 4:31	50	15/9/18 5:36 59	16/9/18 6:41 61	17/9/18 23:46 58	19/9/18 0:51 57	20/9/18 1:56 56
14/9/18 4:36	53	15/9/18 5:41 53	16/9/18 6:46 64	17/9/18 23:51 59	19/9/18 0:56 56	20/9/18 2:01 56
14/9/18 4:41	52	15/9/18 5:46 51	16/9/18 6:51 64	17/9/18 23:56 59	19/9/18 1:01 56	20/9/18 2:06 56
14/9/18 4:46	53	15/9/18 5:51 51	16/9/18 6:56 63	18/9/18 0:01 58	19/9/18 1:06 57	20/9/18 2:11 56
14/9/18 4:51	53	15/9/18 5:56 52	16/9/18 23:01 57	18/9/18 0:06 58	19/9/18 1:11 56	20/9/18 2:16 56
14/9/18 4:56	53	15/9/18 6:01 54	16/9/18 23:06 56	18/9/18 0:11 58	19/9/18 1:16 57	20/9/18 2:21 57
14/9/18 5:01	53	15/9/18 6:06 55	16/9/18 23:11 56	18/9/18 0:16 58	19/9/18 1:21 57	20/9/18 2:26 56
14/9/18 5:06	53	15/9/18 6:11 57	16/9/18 23:16 57	18/9/18 0:21 59	19/9/18 1:26 56	20/9/18 2:31 56
14/9/18 5:11	52	15/9/18 6:16 58	16/9/18 23:21 56	18/9/18 0:26 59	19/9/18 1:31 57	20/9/18 2:36 55
14/9/18 5:16	53	15/9/18 6:21 55	16/9/18 23:26 57	18/9/18 0:31 57	19/9/18 1:36 56	20/9/18 2:41 56
14/9/18 5:21	53	15/9/18 6:26 55	16/9/18 23:31 57	18/9/18 0:36 58	19/9/18 1:41 56	20/9/18 2:46 56
14/9/18 5:26	56	15/9/18 6:31 57	16/9/18 23:36 56	18/9/18 0:41 58	19/9/18 1:46 56	20/9/18 2:51 55
14/9/18 5:31	56 55	15/9/18 6:36 57 15/9/18 6:41 58	16/9/18 23:41 55	18/9/18 0:46 58	19/9/18 1:51 55	20/9/18 2:56 55
14/9/18 5:36	55	15/9/18 6:41 58	16/9/18 23:46 55	18/9/18 0:51 57	19/9/18 1:56 56	20/9/18 3:01 55
14/9/18 5:41	54	15/9/18 6:46 57	16/9/18 23:51 56	18/9/18 0:56 57	19/9/18 2:01 56	20/9/18 3:06 55
14/9/18 5:46	55	15/9/18 6:51 59	16/9/18 23:56 56	18/9/18 1:01 58	19/9/18 2:06 55	20/9/18 3:11 55
14/9/18 5:51	56	15/9/18 6:56 60	17/9/18 0:01 56	18/9/18 1:06 57	19/9/18 2:11 55	20/9/18 3:16 56
14/9/18 5:56	57	15/9/18 23:01 61	17/9/18 0:06 56	18/9/18 1:11 57	19/9/18 2:16 55	20/9/18 3:21 55
14/9/18 6:01	55	15/9/18 23:06 61	17/9/18 0:11 55	18/9/18 1:16 58	19/9/18 2:21 55	20/9/18 3:26 56
14/9/18 6:06	58	15/9/18 23:11 60	17/9/18 0:16 56	18/9/18 1:21 57	19/9/18 2:26 54	20/9/18 3:31 56
14/9/18 6:11	58	15/9/18 23:16 60	17/9/18 0:21 56	18/9/18 1:26 57	19/9/18 2:31 54	20/9/18 3:36 55
14/9/18 6:16	58	15/9/18 23:21 61	17/9/18 0:26 56	18/9/18 1:31 56	19/9/18 2:36 55	20/9/18 3:41 56
14/9/18 6:21	59	15/9/18 23:26 60	17/9/18 0:31 56	18/9/18 1:36 57	19/9/18 2:41 55	20/9/18 3:46 55
14/9/18 6:26	59	15/9/18 23:31 60	17/9/18 0:36 55	18/9/18 1:41 58	19/9/18 2:46 55	20/9/18 3:51 55
14/9/18 6:31	60	15/9/18 23:36 61	17/9/18 0:41 55	18/9/18 1:46 57	19/9/18 2:51 56	20/9/18 3:56 56
14/9/18 6:36	60	15/9/18 23:41 61	17/9/18 0:46 55	18/9/18 1:51 58	19/9/18 2:56 55	20/9/18 4:01 55
14/9/18 6:41	61	15/9/18 23:46 60	17/9/18 0:51 56	18/9/18 1:56 56	19/9/18 3:01 55	20/9/18 4:06 56
14/9/18 6:46	60	15/9/18 23:51 61	17/9/18 0:56 55	18/9/18 2:01 55	19/9/18 3:06 54	20/9/18 4:11 55
14/9/18 6:51	61	15/9/18 23:56 61	17/9/18 1:01 61	18/9/18 2:06 56	19/9/18 3:11 55	20/9/18 4:16 57
14/9/18 6:56	61	16/9/18 0:01 60	17/9/18 1:06 65	18/9/18 2:11 56	19/9/18 3:16 55	20/9/18 4:21 55
14/9/18 23:01	56	16/9/18 0:06 59	17/9/18 1:11 60	18/9/18 2:16 56	19/9/18 3:21 55	20/9/18 4:26 56
14/9/18 23:06	60	16/9/18 0:11 58	17/9/18 1:16 57	18/9/18 2:21 64	19/9/18 3:26 56	20/9/18 4:31 56
14/9/18 23:11	59	16/9/18 0:16 59	17/9/18 1:21 56	18/9/18 2:26 56	19/9/18 3:31 54	20/9/18 4:36 57
14/9/18 23:16	57	16/9/18 0:21 60	17/9/18 1:26 55	18/9/18 2:31 55	19/9/18 3:36 55	20/9/18 4:41 56
14/9/18 23:21	58	16/9/18 0:26 61	17/9/18 1:31 55	18/9/18 2:36 55	19/9/18 3:41 56	20/9/18 4:46 55
14/9/18 23:26	56	16/9/18 0:31 61	17/9/18 1:36 55	18/9/18 2:41 55	19/9/18 3:46 53	20/9/18 4:51 56
14/9/18 23:31	58	16/9/18 0:36 60	17/9/18 1:41 54	18/9/18 2:46 56	19/9/18 3:51 54	20/9/18 4:56 55
14/9/18 23:36	53	16/9/18 0:41 59 16/9/18 0:46 55	17/9/18 1:46 55	18/9/18 2:51 54 18/9/18 2:56 56	19/9/18 3:56 54	20/9/18 5:01 56
14/9/18 23:41	57	16/9/18 0:46 55	17/9/18 1:51 58	18/9/18 3:01 56	19/9/18 4:01 55	20/9/18 5:06 55
14/9/18 23:46	57	16/9/18 0:51 57	17/9/18 1:56 59		19/9/18 4:06 56	20/9/18 5:11 56
14/9/18 23:51	61	16/9/18 0:56 58	17/9/18 2:01 60	18/9/18 3:06 56	19/9/18 4:11 55	20/9/18 5:16 56
14/9/18 23:56	58	16/9/18 1:01 59	17/9/18 2:06 60	18/9/18 3:11 55	19/9/18 4:16 54	20/9/18 5:21 57
15/9/18 0:01	57	16/9/18 1:06 58	17/9/18 2:11 54	18/9/18 3:16 56	19/9/18 4:21 55	20/9/18 5:26 57
15/9/18 0:06	55	16/9/18 1:11 58	17/9/18 2:16 56	18/9/18 3:21 55	19/9/18 4:26 55	20/9/18 5:31 57
15/9/18 0:11	55	16/9/18 1:16 58	17/9/18 2:21 58	18/9/18 3:26 57	19/9/18 4:31 55	20/9/18 5:36 57
15/9/18 0:16	54	16/9/18 1:21 60	17/9/18 2:26 64	18/9/18 3:31 57	19/9/18 4:36 55	20/9/18 5:41 56
15/9/18 0:21	54	16/9/18 1:26 60	17/9/18 2:31 68	18/9/18 3:36 57	19/9/18 4:41 54	20/9/18 5:46 57
15/9/18 0:26	54	16/9/18 1:31 61	17/9/18 2:36 54	18/9/18 3:41 57	19/9/18 4:46 55	20/9/18 5:51 58
15/9/18 0:31	60	16/9/18 1:36 47	17/9/18 2:41 54	18/9/18 3:46 56	19/9/18 4:51 55	20/9/18 5:56 57
15/9/18 0:36	59	16/9/18 1:41 60	17/9/18 2:46 53	18/9/18 3:51 55	19/9/18 4:56 54	20/9/18 6:01 59
15/9/18 0:41	52	16/9/18 1:46 60	17/9/18 2:51 54	18/9/18 3:56 55	19/9/18 5:01 55	20/9/18 6:06 59
15/9/18 0:46	51	16/9/18 1:51 59	17/9/18 2:56 54	18/9/18 4:01 56	19/9/18 5:06 54	20/9/18 6:11 58
15/9/18 0:51	53	16/9/18 1:56 59	17/9/18 3:01 54	18/9/18 4:06 56	19/9/18 5:11 56	20/9/18 6:16 59
15/9/18 0:56	52	16/9/18 2:01 60	17/9/18 3:06 54	18/9/18 4:11 56	19/9/18 5:16 56	20/9/18 6:21 59
15/9/18 1:01	52	16/9/18 2:06 58	17/9/18 3:11 54	18/9/18 4:16 55	19/9/18 5:21 56	20/9/18 6:26 60
15/9/18 1:06	56	16/9/18 2:11 60	17/9/18 3:16 54	18/9/18 4:21 56	19/9/18 5:26 56	20/9/18 6:31 60
15/9/18 1:11	61	16/9/18 2:16 61	17/9/18 3:21 54	18/9/18 4:26 57	19/9/18 5:31 56	20/9/18 6:36 60
15/9/18 1:16	57	16/9/18 2:21 60	17/9/18 3:26 57	18/9/18 4:31 57	19/9/18 5:36 57	20/9/18 6:41 60
15/9/18 1:21	51	16/9/18 2:26 60	17/9/18 3:31 59	18/9/18 4:36 56	19/9/18 5:41 56	20/9/18 6:46 61
15/9/18 1:26	50	16/9/18 2:31 59	17/9/18 3:36 58	18/9/18 4:41 56	19/9/18 5:46 56	20/9/18 6:51 60
15/9/18 1:31	51	16/9/18 2:36 61	17/9/18 3:41 59	18/9/18 4:46 55	19/9/18 5:51 56	20/9/18 6:56 59
15/9/18 1:36	57	16/9/18 2:41 59	17/9/18 3:46 51	18/9/18 4:51 55	19/9/18 5:56 56	20/9/18 23:01 63
	52	16/9/18 2:46 59				

Deal time Naire Date					
Real-time Noise Data 20/9/18 23:11 63	RTN4 (Causeway Bay Communit 22/9/18 0:16 59	ty Centre) 23/9/18 1:21 58	24/9/18 2:26 55	25/9/18 3:31 65	26/9/18 4:36 50
20/9/18 23:16 63	22/9/18 0:21 60	23/9/18 1:26 58	24/9/18 2:31 55	25/9/18 3:36 65	26/9/18 4:41 60
20/9/18 23:21 62 20/9/18 23:26 63	22/9/18 0:26 60 22/9/18 0:31 59	23/9/18 1:31 58 23/9/18 1:36 57	24/9/18 2:36 56 24/9/18 2:41 55	25/9/18 3:41 65 25/9/18 3:46 65	26/9/18 4:46 59 26/9/18 4:51 58
20/9/18 23:31 62	22/9/18 0:36 62	23/9/18 1:41 58	24/9/18 2:46 54	25/9/18 3:51 65	26/9/18 4:56 45
20/9/18 23:36 63 20/9/18 23:41 62	22/9/18 0:41 59 22/9/18 0:46 59	23/9/18 1:46 58 23/9/18 1:51 58	24/9/18 2:51 55 24/9/18 2:56 59	25/9/18 3:56 64 25/9/18 4:01 64	26/9/18 5:01 60 26/9/18 5:06 59
20/9/18 23:46 63	22/9/18 0:51 59	23/9/18 1:56 58	24/9/18 3:01 54	25/9/18 4:06 64	26/9/18 5:11 59
20/9/18 23:51 63 20/9/18 23:56 63	22/9/18 0:56 60 22/9/18 1:01 59	23/9/18 2:01 58 23/9/18 2:06 58	24/9/18 3:06 55 24/9/18 3:11 55	25/9/18 4:11 64	26/9/18 5:16 58 26/9/18 5:21 58
21/9/18 0:01 62	22/9/18 1:06 59	23/9/18 2:00 58	24/9/18 3:16 54	25/9/18 4:16 64 25/9/18 4:21 64	26/9/18 5:21 58 26/9/18 5:26 58
21/9/18 0:06 62	22/9/18 1:11 59	23/9/18 2:16 59	24/9/18 3:21 54	25/9/18 4:26 64	26/9/18 5:31 58
21/9/18 0:11 62 21/9/18 0:16 62	22/9/18 1:16 59 22/9/18 1:21 59	23/9/18 2:21 58 23/9/18 2:26 58	24/9/18 3:26 54 24/9/18 3:31 55	25/9/18 4:31 65 25/9/18 4:36 65	26/9/18 5:36 58 26/9/18 5:41 58
21/9/18 0:21 62	22/9/18 1:26 59	23/9/18 2:31 58	24/9/18 3:36 55	25/9/18 4:41 64	26/9/18 5:46 58
21/9/18 0:26 63 21/9/18 0:31 63	22/9/18 1:31 58 22/9/18 1:36 59	23/9/18 2:36 58 23/9/18 2:41 58	24/9/18 3:41 57 24/9/18 3:46 55	25/9/18 4:46 64 25/9/18 4:51 64	26/9/18 5:51 58 26/9/18 5:56 58
21/9/18 0:36 63	22/9/18 1:41 59	23/9/18 2:46 58	24/9/18 3:51 54	25/9/18 4:56 64	26/9/18 6:01 59
21/9/18 0:41 63 21/9/18 0:46 62	22/9/18 1:46 58 22/9/18 1:51 59	23/9/18 2:51 58 23/9/18 2:56 57	24/9/18 3:56 54 24/9/18 4:01 55	25/9/18 5:01 64 25/9/18 5:06 64	26/9/18 6:06 59 26/9/18 6:11 59
21/9/18 0:51 62	22/9/18 1:56 59	23/9/18 3:01 58	24/9/18 4:06 54	25/9/18 5:10 64	26/9/18 6:16 60
21/9/18 0:56 61	22/9/18 2:01 58	23/9/18 3:06 58	24/9/18 4:11 57	25/9/18 5:16 64	26/9/18 6:21 60
21/9/18 1:01 61 21/9/18 1:06 61	22/9/18 2:06 57 22/9/18 2:11 58	23/9/18 3:11 57 23/9/18 3:16 57	24/9/18 4:16 54 24/9/18 4:21 55	25/9/18 5:21 64 25/9/18 5:26 64	26/9/18 6:26 60 26/9/18 6:31 61
21/9/18 1:11 62	22/9/18 2:16 58	23/9/18 3:21 56	24/9/18 4:26 54	25/9/18 5:31 64	26/9/18 6:36 61
21/9/18 1:16 61 21/9/18 1:21 61	22/9/18 2:21 58 22/9/18 2:26 58	23/9/18 3:26 57 23/9/18 3:31 57	24/9/18 4:31 56 24/9/18 4:36 56	25/9/18 5:36 64 25/9/18 5:41 64	26/9/18 6:41 38 26/9/18 6:46 50
21/9/18 1:26 61	22/9/18 2:31 58	23/9/18 3:36 56	24/9/18 4:41 56	25/9/18 5:46 64	26/9/18 6:51 48
21/9/18 1:31 61 21/9/18 1:36 61	22/9/18 2:36 58 22/9/18 2:41 57	23/9/18 3:41 57 23/9/18 3:46 57	24/9/18 4:46 54 24/9/18 4:51 55	25/9/18 5:51 64 25/9/18 5:56 64	26/9/18 6:56 52 26/9/18 23:01 60
21/9/18 1:41 60	22/9/18 2:46 58	23/9/18 3:51 57	24/9/18 4:56 55	25/9/18 6:01 64	26/9/18 23:06 60
21/9/18 1:46 60	22/9/18 2:51 58	23/9/18 3:56 57	24/9/18 5:01 55	25/9/18 6:06 64	26/9/18 23:11 59
21/9/18 1:51 61 21/9/18 1:56 61	22/9/18 2:56 58 22/9/18 3:01 57	23/9/18 4:01 57 23/9/18 4:06 57	24/9/18 5:06 56 24/9/18 5:11 57	25/9/18 6:11 64 25/9/18 6:16 64	26/9/18 23:16 59 26/9/18 23:21 59
21/9/18 2:01 61	22/9/18 3:06 57	23/9/18 4:11 56	24/9/18 5:16 56	25/9/18 6:21 64	26/9/18 23:26 59
21/9/18 2:06 61	22/9/18 3:11 58	23/9/18 4:16 56 23/9/18 4:21 57	24/9/18 5:21 56	25/9/18 6:26 64	26/9/18 23:31 59 26/9/18 23:36 59
21/9/18 2:11 61 21/9/18 2:16 60	22/9/18 3:16 57 22/9/18 3:21 58	23/9/18 4:21 57 23/9/18 4:26 56	24/9/18 5:26 57 24/9/18 5:31 57	25/9/18 6:31 64 25/9/18 6:36 64	26/9/18 23:36 59 26/9/18 23:41 59
21/9/18 2:21 61	22/9/18 3:26 58	23/9/18 4:31 57	24/9/18 5:36 57	25/9/18 6:41 64	26/9/18 23:46 59
21/9/18 2:26 61 21/9/18 2:31 61	22/9/18 3:31 57 22/9/18 3:36 57	23/9/18 4:36 56 23/9/18 4:41 56	24/9/18 5:41 57 24/9/18 5:46 57	25/9/18 6:46 64 25/9/18 6:51 64	26/9/18 23:51 60 26/9/18 23:56 59
21/9/18 2:36 61	22/9/18 3:41 56	23/9/18 4:46 57	24/9/18 5:51 57	25/9/18 6:56 64	20/9/10/23.30 39
21/9/18 2:41 61	22/9/18 3:46 58	23/9/18 4:51 57	24/9/18 5:56 57	25/9/18 23:01 56	
21/9/18 2:46 61 21/9/18 2:51 61	22/9/18 3:51 58 22/9/18 3:56 58	23/9/18 4:56 55 23/9/18 5:01 56	24/9/18 6:01 57 24/9/18 6:06 58	25/9/18 23:06 53 25/9/18 23:11 54	
21/9/18 2:56 61	22/9/18 4:01 57	23/9/18 5:06 56	24/9/18 6:11 57	25/9/18 23:16 50	
21/9/18 3:01 61 21/9/18 3:06 61	22/9/18 4:06 56 22/9/18 4:11 56	23/9/18 5:11 57 23/9/18 5:16 57	24/9/18 6:16 60 24/9/18 6:21 59	25/9/18 23:21 53 25/9/18 23:26 50	
21/9/18 3:11 60	22/9/18 4:16 56	23/9/18 5:21 56	24/9/18 6:26 59	25/9/18 23:20 50	
21/9/18 3:16 60	22/9/18 4:21 57	23/9/18 5:26 56	24/9/18 6:31 59	25/9/18 23:36 50	
21/9/18 3:21 60 21/9/18 3:26 60	22/9/18 4:26 57 22/9/18 4:31 56	23/9/18 5:31 56 23/9/18 5:36 57	24/9/18 6:36 60 24/9/18 6:41 61	25/9/18 23:41 46 25/9/18 23:46 47	
21/9/18 3:31 60	22/9/18 4:36 58	23/9/18 5:41 56	24/9/18 6:46 60	25/9/18 23:51 47	
21/9/18 3:36 60 21/9/18 3:41 60	22/9/18 4:41 56 22/9/18 4:46 57	23/9/18 5:46 57 23/9/18 5:51 58	24/9/18 6:51 61 24/9/18 6:56 60	25/9/18 23:56 61 26/9/18 0:01 61	
21/9/18 3:41 60 21/9/18 3:46 61	22/9/18 4:46 57 22/9/18 4:51 57	23/9/18 5:51 58 23/9/18 5:56 57	24/9/18 23:01 66	26/9/18 0:01 61 26/9/18 0:06 61	
21/9/18 3:51 60	22/9/18 4:56 57	23/9/18 6:01 58	24/9/18 23:06 66	26/9/18 0:11 61	
21/9/18 3:56 61 21/9/18 4:01 61	22/9/18 5:01 56 22/9/18 5:06 58	23/9/18 6:06 57 23/9/18 6:11 58	24/9/18 23:11 66 24/9/18 23:16 65	26/9/18 0:16 61 26/9/18 0:21 61	
21/9/18 4:06 60	22/9/18 5:11 57	23/9/18 6:16 58	24/9/18 23:21 65	26/9/18 0:26 60	
21/9/18 4:11 60 21/9/18 4:16 60	22/9/18 5:16 57 22/9/18 5:21 58	23/9/18 6:21 59 23/9/18 6:26 59	24/9/18 23:26 66 24/9/18 23:31 66	26/9/18 0:31 38 26/9/18 0:36 60	
21/9/18 4:16 60 21/9/18 4:21 60	22/9/18 5:21 58 22/9/18 5:26 58	23/9/18 6:26 59 23/9/18 6:31 59	24/9/18 23:31 66 24/9/18 23:36 68	26/9/18 0:36 60 26/9/18 0:41 61	
21/9/18 4:26 60	22/9/18 5:31 58	23/9/18 6:36 59	24/9/18 23:41 68	26/9/18 0:46 61	
21/9/18 4:31 60 21/9/18 4:36 60	22/9/18 5:36 58 22/9/18 5:41 58	23/9/18 6:41 59 23/9/18 6:46 59	24/9/18 23:46 68 24/9/18 23:51 68	26/9/18 0:51 60 26/9/18 0:56 60	
21/9/18 4:41 60	22/9/18 5:46 58	23/9/18 6:51 59	24/9/18 23:56 68	26/9/18 1:01 60	
21/9/18 4:46 60 21/9/18 4:51 60	22/9/18 5:51 58 22/9/18 5:56 59	23/9/18 6:56 59 23/9/18 23:01 59	25/9/18 0:01 68 25/9/18 0:06 68	26/9/18 1:06 60 26/9/18 1:11 61	
21/9/18 4:56 60	22/9/18 5:56 59	23/9/18 23:01 59	25/9/18 0:11 68	26/9/18 1:16 61	
21/9/18 5:01 60	22/9/18 6:06 59	23/9/18 23:11 60	25/9/18 0:16 68	26/9/18 1:21 60	
21/9/18 5:06 60 21/9/18 5:11 60	22/9/18 6:11 59 22/9/18 6:16 59	23/9/18 23:16 59 23/9/18 23:21 59	25/9/18 0:21 68 25/9/18 0:26 67	26/9/18 1:26 60 26/9/18 1:31 60	
21/9/18 5:16 60	22/9/18 6:21 59	23/9/18 23:26 58	25/9/18 0:31 67	26/9/18 1:36 61	
21/9/18 5:21 60 21/9/18 5:26 60	22/9/18 6:26 60	23/9/18 23:31 58 23/9/18 23:36 58	25/9/18 0:36 67 25/9/18 0:41 71	26/9/18 1:41 61	
21/9/18 5:26 60 21/9/18 5:31 60	22/9/18 6:31 59 22/9/18 6:36 61	23/9/18 23:41 58	25/9/18 0:46 73	26/9/18 1:46 60 26/9/18 1:51 60	
21/9/18 5:36 60	22/9/18 6:41 59	23/9/18 23:46 58	25/9/18 0:51 72	26/9/18 1:56 60	
21/9/18 5:41 60 21/9/18 5:46 60	22/9/18 6:46 61 22/9/18 6:51 61	23/9/18 23:51 58 23/9/18 23:56 58	25/9/18 0:56 70 25/9/18 1:01 70	26/9/18 2:01 60 26/9/18 2:06 60	
21/9/18 5:51 61	22/9/18 6:56 61	24/9/18 0:01 57	25/9/18 1:06 68	26/9/18 2:11 60	
21/9/18 5:56 61 21/9/18 6:01 61	22/9/18 23:01 61 22/9/18 23:06 60	24/9/18 0:06 58 24/9/18 0:11 59	25/9/18 1:11 68 25/9/18 1:16 66	26/9/18 2:16 60 26/9/18 2:21 60	
21/9/18 6:06 61	22/9/18 23:11 60	24/9/18 0:16 57	25/9/18 1:21 66	26/9/18 2:26 60	
21/9/18 6:11 61	22/9/18 23:16 61	24/9/18 0:21 58	25/9/18 1:26 66	26/9/18 2:31 60	
21/9/18 6:16 62 21/9/18 6:21 62	22/9/18 23:21 60 22/9/18 23:26 60	24/9/18 0:26 57 24/9/18 0:31 58	25/9/18 1:31 66 25/9/18 1:36 66	26/9/18 2:36 60 26/9/18 2:41 60	
21/9/18 6:26 62	22/9/18 23:31 60	24/9/18 0:36 57	25/9/18 1:41 67	26/9/18 2:46 60	
21/9/18 6:31 62 21/9/18 6:36 62	22/9/18 23:36 60 22/9/18 23:41 60	24/9/18 0:41 56 24/9/18 0:46 57	25/9/18 1:46 66 25/9/18 1:51 66	26/9/18 2:51 60 26/9/18 2:56 60	
21/9/18 6:41 63	22/9/18 23:46 60	24/9/18 0:51 57	25/9/18 1:56 66	26/9/18 3:01 60	
21/9/18 6:46 62	22/9/18 23:51 60	24/9/18 0:56 57	25/9/18 2:01 67	26/9/18 3:06 60	
21/9/18 6:51 62 21/9/18 6:56 63	22/9/18 23:56 60 23/9/18 0:01 59	24/9/18 1:01 58 24/9/18 1:06 57	25/9/18 2:06 67 25/9/18 2:11 69	26/9/18 3:11 60 26/9/18 3:16 58	
21/9/18 23:01 61	23/9/18 0:06 59	24/9/18 1:11 57	25/9/18 2:16 68	26/9/18 3:21 62	
21/9/18 23:06 61 21/9/18 23:11 62	23/9/18 0:11 59 23/9/18 0:16 60	24/9/18 1:16 56 24/9/18 1:21 57	25/9/18 2:21 66 25/9/18 2:26 66	26/9/18 3:26 62 26/9/18 3:31 63	
21/9/18 23:16 60	23/9/18 0:21 59	24/9/18 1:26 57	25/9/18 2:31 69	26/9/18 3:31 63	
21/9/18 23:21 61	23/9/18 0:26 60	24/9/18 1:31 55	25/9/18 2:36 68	26/9/18 3:41 63	
21/9/18 23:26 60 21/9/18 23:31 60	23/9/18 0:31 60 23/9/18 0:36 59	24/9/18 1:36 56 24/9/18 1:41 56	25/9/18 2:41 67 25/9/18 2:46 66	26/9/18 3:46 62 26/9/18 3:51 62	
21/9/18 23:36 60	23/9/18 0:41 61	24/9/18 1:46 55	25/9/18 2:51 66	26/9/18 3:56 62	
21/9/18 23:41 60	23/9/18 0:46 59 23/9/18 0:51 59	24/9/18 1:51 57 24/9/18 1:56 55	25/9/18 2:56 66 25/9/18 3:01 66	26/9/18 4:01 62	
21/9/18 23:46 60 21/9/18 23:51 60	23/9/18 0:51 59 23/9/18 0:56 59	24/9/18 1:56 55 24/9/18 2:01 55	25/9/18 3:01 66 25/9/18 3:06 66	26/9/18 4:06 62 26/9/18 4:11 62	
21/9/18 23:56 60	23/9/18 1:01 59	24/9/18 2:06 54	25/9/18 3:11 66	26/9/18 4:16 61	
22/9/18 0:01 60 22/9/18 0:06 60	23/9/18 1:06 59 23/9/18 1:11 59	24/9/18 2:11 54 24/9/18 2:16 56	25/9/18 3:16 65 25/9/18 3:21 65	26/9/18 4:21 62 26/9/18 4:26 62	
22/9/18 0:11 60	23/9/18 1:16 58	24/9/18 2:21 55	25/9/18 3:26 65	26/9/18 4:31 61	ļ

am


Contract no. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

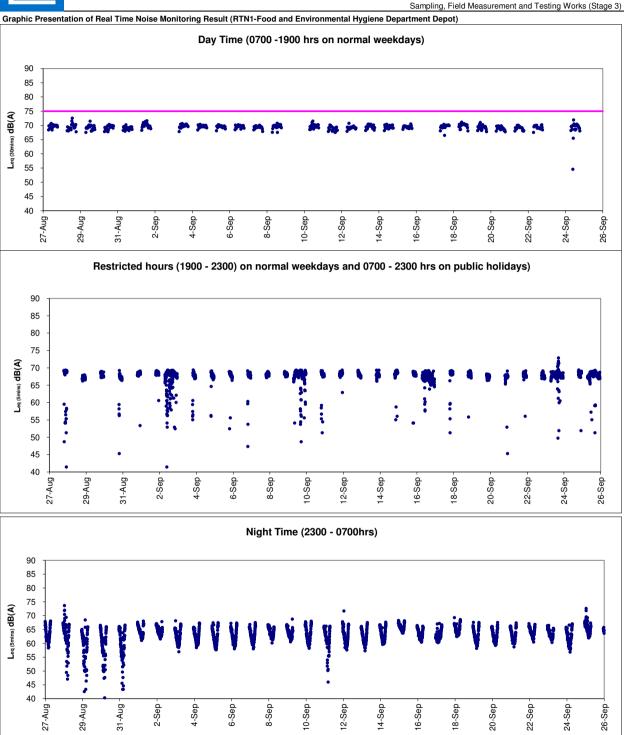




Contract no. HK/2015/01 Wan Chai Development Phase II and Central -Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)







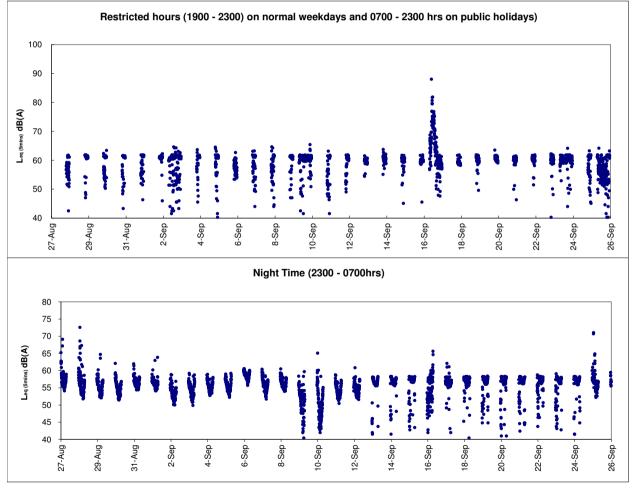




Contract no. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

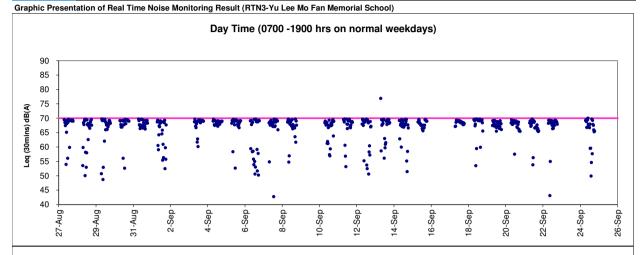

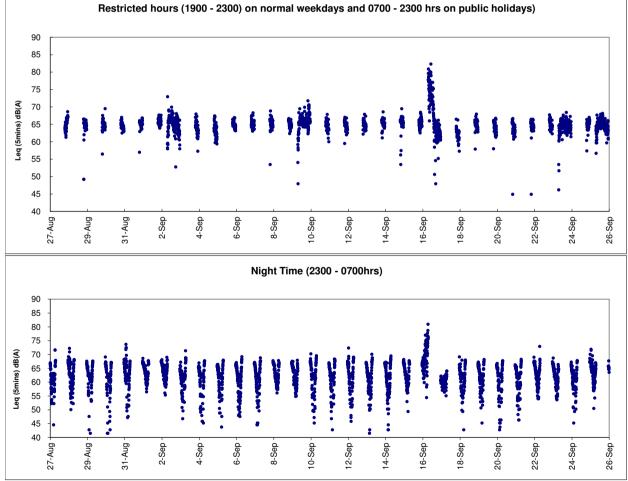



Contract no. HK/2015/01 Wan Chai Development Phase II and Central-Wan Chai Bypass Sampling, Field Measurement and Testing Works (Stage 3)

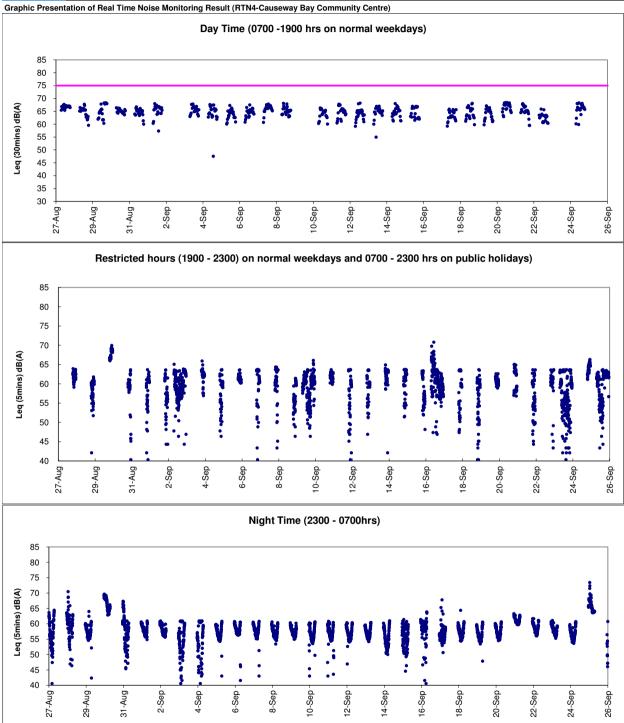



Appendix 6.1

Event Action Plans



Event/Action Plan for Construction Noise

EVENT		A	CTION	
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	 Notify ER, IEC and Contractor; Carry out investigation; Report the results of investigation to the IEC, ER and Contractor; Discuss with the IEC and Contractor on remedial measures required; Increase monitoring frequency to check mitigation effectiveness. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Review the investigation results submitted by the ET; Review the proposed remedial measures by the Contractor and advise the ER accordingly; Advise the ER on the effectiveness of the proposed remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Supervise the implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Submit noise mitigation proposals to IEC and ER; Implement noise mitigation proposals. (The above actions should be taken within 2 working days after the exceedance is identified)



EVENT		ACTION	
	ET	IEC ER	CONTRACTOR
Limit Level being exceeded	 Inform IEC, ER, Contractor and EPD; Repeat measurements to confirm findings; Increase monitoring frequency; Identify source and investigate the cause of exceedance; Carry out analysis of Contractor's working procedures; Discuss with the IEC, Contractor and ER on remedial measures required; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. The above actions should be taken within 2 working days after the exceedance is identified) 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. The above actions should be taken within 2 workin g days after the exceedance is identified) If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. The above actions should be taken within 2 workin g days after the exceedance is identified) If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance is abated. The above actions should be taken within 2 working days afte the exceedance is identified) 	 avoid further exceedance; Submit proposals for remedial actions to IEC and ER within 3 working days of notification; Implement the agreed proposals; Submit further proposal if problem still not under control; Stop the relevant portion of works as instructed by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is



Event / Action Plan for Construction Air Quality

EVENT	ACTION						
	ET	IEC	ER	CONTRACTOR			
ACTION LEVEL							
1. Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER; Repeat measurement to confirm finding; Increase monitoring frequency to daily. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Check monitoring data submitted by ET; Check Contractor's working method. (The above actions should be taken within 2 working days after the exceedance is identified) 	Notify Contractor. (The above actions should be taken within 2 working days after the exceedance is identified)	 Rectify any unacceptable practice; Amend working methods if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified) 			
2. Exceedance for two or more consecutive samples	 Identify source; Inform IEC and ER; Advise the ER on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with IEC and ER; If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Submit proposals for remedial to ER within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified) 			
LIMIT LEVEL							
1. Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate. (The above actions should be taken within 2 working days after the exceedance is identified) 			
2. Exceedance for two or more consecutive samples	 Notify IEC, ER, Contractor and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and ER to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Discuss amongst ER, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified) 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within 3 working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified) 			



Appendix 6.2

Summary for Notification of Exceedance



Ref. No.	Date	Time	Location	Construction Noise Level, dB(A)	Parameter	Action Level	Limit Level dB(A)	Follow-up action	
-	-	-	-	-	-	-	-	-	-



Appendix 9.1

Complaint Log



Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
110723a	23/07/2011	Ms. Law at Victoria Centre by ICC no. 1- 303887687	North Point	She concerned that Highways Department published a notice in their Management Office about construction works will be conducted from 0700 hours to 2300 hours during July to December 2011 including Saturday, Sunday and public holiday.	 It was referred by AECOM to ET on 28 July 2011 RSS confirmed that the notice was prepared by Victoria Centre 'a Management office to their resident and the advice was only given on the extension construction works (for Contract HY/2009/15) to 7am-9pm Monday to Saturday except Public Holidays and Sundays. As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid- August 2011. No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 19 and 25 July 2011 during daytime and evening time period while breaking and excavation works were observed during monitoring. In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures. 	Closed
110723b	23/07/2011	Ms. Yau at Block 2, Victoria Centre by ICC no. 1- 304013959	North Point	Reclamation work was conducted at Causeway Bay Typhoon Shelter at 7am on 23 July 2011. She complained that the works shall be started later to minimize the noise nuisance to the vicinity of the residents in early morning	 It was referred by AECOM to ET on 8 August 2011 RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents. With reference to the construction noise monitoring at Victoria Centre, no exceedance was recorded on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures. 	Closed
110727a	27/07/2011	Mr. Law from Victoria Centre Management Office by ICC no. 1-304616162	North Point	It was complained by Mr. Law from Victoria Centre Management Office on 27 July 2011 regarding construction noise generated by the construction operations of	 It was referred by AECOM to ET on 28 July 2011 RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents. No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 25 July and 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Central-Wanchai Bypass at noon rather than in morning at 7am.	 4 August 2011 during daytime and evening time period while breaking and excavation works were observed during monitoring. 5) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. No further complaint from complainant was received after proposed the mitigation measure. 	
	27/07/2011	Ms. Chiu by ICC no.1-304615409	North Point	Noise nuisance from the excavation works for the Highways Department adjacent to the Victoria Centre was conducted from 7am	 It was referred by AECOM to ET on 28 July 2011 With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 25 July and 4 and 10 August 2011 during daytime while breaking and excavation works were undertaken during monitoring. As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am. 	Closed
	07/08/2011				 4) However, complainant did not satisfy with the response on the noise nuisance from the rock-breaking during morning in front of Victoria Centre and then further complaint via 1823 on 7 August 2011. 5) Highways contacted the complainant on 15 August 2011 that the noisy rock breaking operation had been completed. 	
110730	30/07/2011	Mr. Tsui by ICC no. 1-305074350	Central	Construction noise generated by operations of Central- Interchange which is near the spa room at Four-Season Hotel. Also, the complaint enquired the commencement time of the construction on Saturday.	 Remarks: There will be counted as two complaints in this complaint log. 1) It was referred by AECOM to ET on 1 August 2011. 2) RSS confirmed that noisy plants from 2 vibratory hammers have been conducted in alternating manner for piling and drilling works for diaphragm wall construction. 3) With reference to the construction noise monitoring at IFC Western End of Podium, no exceedance was recorded on 4 August 2011 during monitoring while sheet piling works were undertaken during monitoring. 4) In order to reduce the noise impact to nearby noise sensitive receivers, Contractor has been implemented the following noise mitigation measures: Erection of acoustic lining at the hoarding next to Four Seasons Hotel; Temporary noise barrier with extended acoustic lining; 	Closed
					following noise mitigation measures: - Erection of acoustic lining at the hoarding next to Four Seasons Hotel; - Temporary noise barrier with extended acoustic	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Seasons Hotel instead of 2 5) In conclusion, it was related to the construction works under Contract HY/2009/18 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.	
110810	10/08/2011	Mr. Yip by ICC no. 1 – 306740207	North Point	Muddy water was discharged from work site to the seafront near Oil Street during heavy rain. The environmental protection measures were not good enough and are needed to rectify.	 It was referred by AECOM to ET on 17 August 2011. Confirmed with RE, Muddy water was caused by a heap of earth being washed to the sea by heavy rain. The heap of earth was referred as a small stockpile placed close to the seafront in front of Oil Street within the site area under handover transition period from contract HY/2009/11 to contract HY/2009/19. The necessary mitigation measures to protect the small stockpile against rainfall were missing at the time of complaint. Due to the missing of mitigation measures to protect the small stockpile during handover transition period, loose material was washed into the harbour when heavy rain came. Muddy water was formed and dispersed in the sea that caused the water quality and visual concern to the public. The complaint was considered as valid. Contractors were advised to relocate the loose materials away from the coastline as far as practicable. Any loose material placed which needed to be placed near the coastline shall be properly compacted or covered as appropriate. To avoid any further environmental deficiency, Contractors shall ensure all necessary environmental mitigation measures will not be missing during site area handover. 	
110817	17/08/2011	ICC no. 1- 307657681	North Point	Visual impact generated by light from a large amount of spot-lights on the barge during mid-night nearby City Garden.	 It was referred by AECOM to ET on 23 August 2011 RSS confirmed that some non-essential lights were turned on during night-time period which caused the nuisance to the nearby residents. In addition, absence of lighting shields at flood lights results in visual glare to the complaint at night-time. Follow-up action had been taken by contractor that switches off all non-essential lights to minimized nuisance to the nearby residents. The complainant satisfied to the practice and no further complaint was received after that. 	Closed
110826	26/08/2011	Grand Hyatt and a complainant by ICC	Wan Chai	Construction noise and vibration nuisance generated from the works at Convention Avenue and inside the HKCEC1	 Confirmed with the Resident Site Staff that the construction works were referred to the Contractor HK/2009/01. The Excavator mounted breaker at Convention Avenue 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				reclamation area.	 and Drilling rig at HKCEC1 reclamation area were the dominant construction noise source during this period. 3) The drilling rig at HKCEC1 reclamation area and excavator mounted breaker at Convention Avenue were then temporary suspended after received the complaint. 4) Investigation revealed that the erected noise barrier (4m cantilevered movable noise barrier for the drilling rig and 1m movable noise barrier for the excavator mounted breaker) were not located close to the plants to provide adequate noise screening. 5) Contractor was advised to avoid concurrent operation of construction plants at site. Further enhancement of movable noise barriers at HKCEC1 and providing noise enclosure for the excavator mounted breaker at Convention Avenue are needed. 6) Further site investigation and checking on 31 August and 7 September 2011 revealed that the implemented noise mitigation measures were in proper and minimize the noise impact. 	
110826A	26/08/2011	A complaint letter from Mr. Au of Cayley Property of City Garden	North Point	Harbor front adjacent to their water intake suction which caused 3 times of system breakdown of the sea water pump on 9, 22 and 25 August 2011.	 It was referred by AECOM to ET on 29 August 2011 Confirmed with the Resident Site Staff that the construction works were referred to the Contractors HY/2009/11 and HY/2009/19. The pump is located on the site area of HY/2009/19 A temporary garbage defender was installed on 23 July 2011 by HY/2009/11 and the shape of the defender was adjusted on 8 August 2011 in order to excluse the outfall. An ad hoc inspection of the effectiveness of garbage defender was conducted with RSS (CWB project team), contractor of HY/200911 and HY/2009/19 and IECon 29 August 2011. Inspection report of it was submitted to RSS on 19 September 2011. Daily cleaning near the water intake was conducted twice a day by contractor HY/2009/19. In response to City Garden request, the contractors have set up the temporary garbage defender in function and collect the floating refuses, but cannot eliminate all refuses, in particular the refuse come from sea bed from entering the intake. According to the complaint letter from Cayley Property, the outcomes of the preventive measures were not complying with their expectation. During on-site inspection, floating refuses observed 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
111014	14/10/2011	The complainant, Ms. Tam complained via hotline 1823	Wan Chai	The polluted fumes and exhaust from the excavation by sub-contractor of CEDD on pedestrian way outside no.25 Harbour Road (in front of the Harbour Centre)	 occasionally outside the garbage defender. No conclusion could be made for the source of these floating refuses. On the other hand, some of the floating refuses were observed immigrating in the protective zone during investigation 8) All daily cleaning actions had been taken by contractor to minimize floating refuse inside the construction site. It was noted that the intake (land side) is open assess to public, so that many activities such as fishing, feeding fish were conducted there even though a notice has already hoisted. Also, tripping of rubbish by the passers-by could result in a lot of rubbish accumulated around the intake point. 9) Referring to the record provided by CPML, there were a lot of nylon/ plastic bags and nylon wire mesh that matched those rubbishes generated from the public activities. 10) Contractors have fulfilled the requirement of site cleanness and no exceedance was recorded during Water Quality Monitoring. It is consider the cause of this complaint is not related to project and environmental issue in this project as well. No more complaint received after ad-hoc inspection 11) RSS notified ET to carry out investigation on 17 October 2011. 2) ET confirmed with the Resident Site Staff that the location of the excavator was within site area of Contract no. HK/2009/02 undertaking the water cooling main reprovision works along the Harbour Road. The plants including the excavator have been checked before using at the site. However, the polluted fumes and exhausted from the excavator was caused due to insufficient maintenance of the plant after using at site. 3) After receiving the complaint, the excavator was then removal off-site for checking and maintenance works on 17 October 2011. 4) Contractor was reminded to enhance regular checking and maintenance to all plants at site. 5) RSS has replied to the complainant on the arrangement of the measures taken on 17 October 2011. Complainant was satisfied with the res	
111104	04/11/2011	Mr. Liu from	Wan Chai	Complain about a tree near the	by the Contractor. 1) ET confirmed with the Resident Site Staff that	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		LCSD complained via Contractor Complaint Hotline		site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road, the status is not healthy and roof ball of two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue were half cut.	 A tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road is the Tree no. TA1122 under Contract no. HK/2009/02. Leaves of a branch of this tree were shrivelled. Two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue are the tree nos. A160 and A161 under Contract no. HK/2009/01. Part of roof ball of these two trees was covered by the metal plate. 2) Independent Tree Specialists for these two inspected the trees. Contractor HK/2009/01 has taken the measure as recommend downgrading the soil level around the trunk base. Reinstating of the ground works will be conducted in mid-December 2011. For the tree no. TA1122 under Contract no. HK/2009/02, the brown leaves were removed and fenced the tree with orange net is provided to prevent damage of tree trunk by construction works. The distance between the tree and the edge of the trench is kept approximate 2m. Two Contractors were reminded to carry out regular watering to the trees within their site area. 	
111106	06/11/2011	Police officer	Wan Chai	Construction noise generated from the site at about 6:30 a.m on 6 November 2011 and require to stop the machine operation	 According to the information reported by Contractor, one BC cutter and hoist were operated for Diaphragm Wall construction of Shatin-Central Link to inspect bentonite pipes and ensure no damages and all the joints are tightened in good position. Then, the subcontractor for Diaphragm wall, SAMBO Korean foreman stopped the engine of the BC cutter immediately. The police officer recorded the details and HKID number of the foreman and then left. Due to the different language communication between the police officer and the Korean foreman, no CNP was checked by the police officer. ET confirmed with the Resident Site Staff that same issue was also raised out by RSS at about 7:00a.m on the same day. Besides, it was confirmed that there is no valid Construction Noise Permit for the conducted construction works in the period between 2300 and 0700. Due to insufficient communication between Contractor HK/2009/01 and their Korean Sub-contractor, Korean Sub-contractor had not notified to Contractor before carrying out the inspection of the BC cutter, hoists and 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					 bentonite pipes at about 6:00a.m to ensure no damages and all the pipe joints should be tightened and in good position. 4) Contractor was advised to enhance the communication between Contractor and sub-contractor and provide sufficient environmental training to all foreman and operators on restricted hour operation. Futhermore, Construction Noise Permit should be checked and in place for the construction works during restricted hour 5) This complaint was considered in relation to the conducted construction Noise Permit. No more construction works were conducted during night time period. The construction works will be conducted in accordance with the time period stated in valid CNP. This complaint will be kept in view of any follow-up action from the relevant government activities. 	
111212	12/12/2011	The complainant, Mr Tsui from IFCII's management office complained via hotline 1823	Central	A visual impact complaint from hotline 1823 was received by ET on 9 January 2011 (ICC Ref. No.: ICC#1-333037096 dated on 12 December 2011). The complaint, Mr Tsui was reported that visual nuisance caused by lighting in the construction site during night time.	 RSS notified ET on 9 Jan 2012. ET confirmed with the Resident Site Staff that A joint inspection was conducted by Mr Tsui and contractor on that night to see whether there is any improvement. Due to safety reason, igniting enought lights should not be avoided in construction site. However, the light sources were not directed away from pointing to the sensitive receiver and results in visual glare to the complaint. Confirmed with the Resident Site Staff the complainant was satisfied the new arrangement of the lights with contractor after the joint inspection. No further complaint received after that. 	Closed
111220	20/12/2011	The complainant, Ms. Poon complained via hotline 1823 (ICC Ref. No.: ICC#1- 334683841)	North Point	Construction air and noise nuisance generated that many trucks carrying construction materials driving along Watson Road and Oil Street and possibly entering/leaving the construction site near the IEC during 0800 to 1900 hours.	 RSS notified ET on 22 Dec 2011. ET confirmed with the Resident Site Staff that the complainant cannot identify whether the trucks were working under the CWB project or not. The dominant construction air and noise nuisances were emitted by the trucks along Oil Street and Waston Road, however, this is the public road for all vechicles. Reviewing the air qualiuty montioring and noise monitoring results. No exceedance was recorded during this period. Confirmed with the Resident Site Staff that they provided a contact no. for any future enquiries regarding 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					CWB project to the complainant and she was satisfied on the arrangement and no further complaint was received after that.	
111230	30/12/2011	Residents of Harbour Heights	North Point	Construction air and noise nuisance generated by construction vehicles were found parked illegally at King Wah Poad and lining up at Oil Street without the engine turning off.	 RSS notified ET on 6 January 2011. ET confirmed with the Resident Site Staff that a number of construction activities are concurrently proceeding in the vicinity of Oil Street, King Wah Street and a private development project in King Wah Street The dominant construction air and noise nuisances were emitted by the trucks along Oil Street and King Wah Road, however, this is the public road for all vechicles. Reviewing the results of air quality montioring station (CMA1b) and noise monitoring (M4b). No exceedance was recorded during this period. Site inspections for HY/2009/19 were conducted on 4 January 2012. The condition of the site access at Oil Street and the public road nearby were found satisfactory. It is noted that HyD also allow and encourage their contractors to maximize the use of marine access, where available, to work sites, so as to minimize burdening nearby public roads. When land trips are unavoidable, they require contractors to tidy up their construction vehicles before leaving works sites. No contractor under CWB project parked their vehicles illegally at King Wah Street, and HyD still reminded them not to commit such offence. According to HyD's staff replied the complaint letter on 10 January 2012, there is a private development project under construction at King Wah Road. To access these works sites, construction vehicles have to use public roads nearby. No further complaint received after HyD's reply. 	Closed
120118	18/01/2012	N/A	North Point	A complaint regarding a tree located in front of Victoria Centre under IECL was covered by one meter mud without any protection. The complainant concerns the health of the tree in such condition.	 1) RSS notified ET on 20 January 2012. 2) ET confirmed with the Resident Site Staff that The tree is inside the site area of HY/2009/19 and The Botanical name of the tree is Ficus superba var. japonica and the I.D. of the tree is UT48 3) According to the information provided by RSS on 20 Jan 2012, the tree shall be felled that has been approved by DLO on 29 August 2011. Moreover, the tree was felled 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					by contractor on 19 January 2012. 4) No further complaint received after HyD's reply.	
120305	03/03/2012	Resident of Harbour Heights complained via hotline 1823 (ICC Ref. No.: ICC#1- 344632511)	North Point	A complaint regarding excessive noise from construction sites of CWB was observed outside Harbour Heights from Monday to Saturday before 8am. The plants were frequently turned on before 7:30am creating nuisance. The complainant requested a speedy follow-up and reply from relevant department.	 ET confirmed with the Resident Site Staff that PME for diaphragm wall construction started to operate at about 7:30am whilst the other PME, including those for land bored piling work, started to operate after 8am. 	
120405	05/04/2012	N/A	North Point	A complaint regarding excessive noise from construction sites of CBTS was observed daily before 7:30am except on public holidays, and the noise source was mainly from piling works. The complainant requested that construction works should start after 8:30am to avoid nuisance to nearby residents and a speedy follow-up and reply.	 ET confirmed with the Resident Site Staff that no piling works were performed during the concerned period. 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					2012 via 1823. HyD replied that the current of CBTS were drilling, diaphragm wall construct deep excavations. In order to minimize the generated from the above works, the Contra erected temporary noise barriers and provide blankets on plants. RSS would continue to we the Contractor on the effectiveness environmental mitigation measures implements site. No further complaint was received a response.	on and e noise tor had d noise ork with of the ited on
120415	15/04/2012	The complainant Ms. Law, resident of Fu Lee Loy Mansion, complained via hotline 1823 (ICC Ref. No.: 1- 351021108)	North Point	A complaint regarding excessive noise generated from a HyD project that is located at the connection point of CWB and IEC affecting nearby residents. Lately during the middle of the night (around 00:00 to 05:00), low frequency noise, which possibly came from the operating power generator and the barges which were parked along the Oil Street work site, were making a nuisance to the complainant and residents nearby. The complainant requested that relevant department should follow-up.	 ET confirmed with the Resident Site Staff th was no operation of power generators for HY/ and HY/2009/17 (HY/2009/11 had no physic on site) during the concerned period. Althou were a few barges mooring at the sea HY/2009/19, they were not in operation and h operational paics would be omitted 	2009/19 al work h there ront of ence no g (M4b ng day 5dB(A). d on 18 tigation found tion of 2009/17 ring the barges rere not ould be 0 April t works tunnel ndation rerations rch and nd so it as not at, RSS on the immental not to



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130308	06/03/2013	ICC Case#1- 407181502	Tin Hau	A complaint regarding the dropping of fine rock material into surrounding waterbody was observed during rock breaking operation with two excavators in active operation at the Eastern Breakwater of Causeway Bay Typhoon Shelter near the North Point lighthouse.	 RSS notified ET on 8 Marc 2013 ET confirmed with RSS that excavation works, installation of buoy, flashing light and silt curtain and dredging works were undertaken at Eastern Breakwater during the concerned period on 6 March 2013. One backhoe was at idle during the concerned period on 6 March 2013. Reviewing the photo record provided by RSS, the condition of the silt curtain deployed around the Eastern Breakwater on 6 March 2013 was found to be in good condition. It is considered that the silt curtain was properly in place during the concerned period and the concerned act of dropping of fine rock material was confined within the silt curtain boundary without adverse impact to the nearby water quality. Further follow up was conducted on 12 March 2013 during weekly environmental audit inspection, the silt curtain deployed around the concerned area was found to be maintained in good condition and the water quality at the concerned work area was generally satisfactory. No violation of the Environmental Permit condition was found. The contracotr was advised and committed to implement preventive meaures to miminize the potential impact of work including conducting regular diver check to ensure the integrity and the extend of silt curtain deployment and to provide adequtae back up stock of silt curtain for emergency use. 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130606	30/5/2013	ICC Ref. No.: #1- 430164728	Central – Man Kat Street	1. A number of trees (approximately more than ten) along Man Kat Street were found to be in poor health condition with withered and yellow leaves. The complainant has requested a follow-up by relevant department.	 1) RSS notify ET on 6 June 2013 2) ET confirmed with the Resident Site Staff that According to the information provided by RSS, 13 no. of the trees - Roystonea regia (T1674, T1675, T1676, T1677, T1678, T1679, T1680, T1681, T1683, T1644, T1643, T1641, T1639) at the concerned location raised by the complainant was found to be with withered and yellow leaves and 1 no. of tree- Khaya senegalensis (T1712) raised by the complainant was found to be with withered and yellow leaves and 1 no. of tree- Khaya senegalensis (T1712) raised by the complainant was found to be in poor health condition. No construction works was undertaken by Contract HY/2009/18 at the concerned planter area where the affected trees are located. It was also observed that an active CEDD construction works area under a separate contractor not related to Central Wan Chai Bypass Project was found to be located within the concerned planter area. 3) A follow-up joint inspection with RSS and Landscape specialist was conducted on 10 June2013, it was considered that the witered and yellow leaves of the affected trees (T1674,T1675,T1676,T1677,T1678,T1679,T1680,T1681, T1683,T1644,T1643,T1641,T1639) at the concerned planter area were contributed by natrual life cycle of the affected trees and the health condition of the affected trees were considered to be fair. It was also noted that an active CEDD works area was located within the concerned planter area in close proximity to few of the concerned planter area in close proximity to few of the concerned planter area in close proximity to few of the concerned trees (T1644,T1643,T1641,T1639) Accord	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
	Complaint		Complainant		 During the follow-up inspection on 10 June 2013, It was observed that construction material and oil drum were placed near the the roots area of other trees within the CEDD works. Despite the above observation, no direct evidence was found on site which indicates the work front have contributed to the poor health condition of the affected tree (T1712) at the time of investigation. 4) The relevant contractor have removed the construction material near the root area of the trees retained on site and conduct pruning to remove the withered and yellow leaves retained on tree trunk to minimize impact on the trees appearance. In addition, safety supporting wire was provided for concerned tree (T1712) 5) ET recommended the contractor to keep in view the health condition of the concerned tree (T1712) and apply permission for tree felling together with tree compensation plan if considered necessary. Furthermore, the contractor was reminded to implement regular checking of tree health condition and regular removal of withered leaves to maintain the overall tree appearance. 	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
130611	30 May 2013 and 1 June 2013	EPD Ref.:H04/RS/0001 1587-13	Area near Central Pier	1. Noise was emanated from the construction site near the Central Piers at around 0900 hrs on 30 May 2013 and other days and requested follow up action by relevant department.	 1) RSS notify ET on 11 June 2013 2) ET confirmed with the Resident Site Staff that According the information confirmed by RSS, major noise generating construction activities undertaken at works area near Central Pier during the concerned time include Breaking up existing D-wall concrete and excavation at portion 4B and 4C Sheet pilling works at Portion VI (Man Kat Street) 3) Total 1 no. of Backhoe with breaker, 1 no. of Backhoe with vibratory hammer and 4 no.s of pneumatic breakers were deployed for the above construction activities. Reviewing the noise monitoring data at monitoring stations (M7e- International Finance Centre Western End of Podium), no limit level exceedances were recorded during routine noise monitoring period, the noise emanated from the construction activities under Contract HY/2009/18 was considered to complied with the statutory requirement. In addition, weekly environmental site inspection was conducted on 30 May 2013 at around 10:00. According to the inspection record, no particular observation regarding noise impact was recorded and the mitigation measures including erection of of temporary noise barrier was observed in place. As such, no direct information associated with the noise concerned raised was considered available and no non-conformity was identified. 4) ET recommend the contractor to review the need of additional noise mitigation measures to further reduce the noise emmated during construction works for pier side public area. 	Interim report submitted to EPD on 19 June 2013, EPD advised no further comment on 5 Aug 2013and final report for case closing submitted on 6 Aug 2013.



	Date of complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
131010 03 20	3 Oct 013	ICC Ref: No.1- 467000768	Area between Central Pier and International Finance Centre	Noise and air quality impact was experienced at the area located between IFC and Central Pier during peak hours.	 ET confirmed with the Resident Site Staff that 1) The major construction activities at the concerned location conducted over the past three months include; Formwork, rebar and concreting Backfilling Water-proofing Scaffolding erection 2) Mitgitation measures implemented by the Contractor for the above construction works include Select quiet plant and work methods; Check plant and equipment for condition; For use of powered mechanical equipment during restricted hours: Obtain necessary Construction Noise Permit and strictly comply with their conditions; Frequently spray water to major haul road and stockpiles to suppress dust generation; and Cover stockpiles with impervious sheets The construction activities including backfilling, concreting and other assoicated tunnel works were undertaken in the past three months. Having reviewing the monitoring data of the monitoring stations in the vincinity of the concerned location raised by the complainant, namely monitoring station M7e and M7w (Noise Monitoring Station) and MA1e and MA1w (Air Monitoring Station), no action or limit level exceedance was recorded. 	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Elevated noise level at monitoring station M7e (International Finance Centre East Podium) was noted on 24 September 2013. The Contractor is recommended to review the current measures and to implement additional noise mitigation measures to further avoid potential impact to nearby public area during construction works.	
131217	16 Dec 2013	ICC Case Ref.: 1- 484998552	Victoria Park near Hing Fat Street Exit	Sweeping of muddy water into public drains.	 ET confirmed with the Resident Site Staff that 1) The major construction activities around the concerned location conducted on 16 Dec 2013 a.m.includes: -Preparation work of rootball for tree transplanting According to the information provided by RSS, the construction activities around the concerned location on 16 Dec 2013 include preparation work of rootball for tree transplanting at Zone 17/18. A further investigation on the complaint was conducted on 19 Dec 2013 during weekly environmental inspection. It was observed that a tree worksarea comprised of mainly loosen soil was located near the concerned location. It was considered that the inclined surface and loosen soil nature of the concerned worksarea could have led to the muddy surface runoff in rain. Deposition of muddy runoff onto nearby public pavement outside worksarea was hence resulted and was subsequently cleaned into nearby public stormwater drain by the Contractor's workers on the complaint date. As such, the case was considered as works related. Sandbags, geotextile and gravels were immediately placed by the Contractor around the gullies at the concerned location to prevent leftover muddy runoff to the public stormwater drain as observed during the weekly inspection on 19 Dec 2013. With respect to the follow-up raised by the complainant on 19 Dec 2013, sandbags, geotextile and gravels placed at gullies located at public area were removed by the Contractor on the same day for maintaining passible public pavement. Follow up measures including sandbag bundle and covering of worksarea with impervious sheeting was immediately placed at the source of impact at the concerned worksarea boundary by the Contractor. 	Final investigation report issued on 20 Dec 2013. Case closed on 3 Jan 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
131224	24 Dec 2013	(ICC Case Ref.: 1-486434321	Victoria Park Children Playground	Odour and large amount of dust particles affecting the public user of the Victoria Park near Children playground	 ET confirmed with the Resident Site Staff that 1) The major construction activities around the concerned location conducted on 24 Dec 2013 include: Breaking up exisiting pillar box for new children playground Portion II Pressing of sheet pile at bowling green for ELS works Portion XII Welding work for preparation of sheetpiling work at bowling green Portion VI Demolition of existing pavilion for bowling green Portion VI Felling of tree TA50 at Victoria Park Zone 2) Mitgitation measures implemented by the Contractor for the above construction works include Water spraying for demolition and other dust generating works. According to the relevant site records, breaking up of existing pillar box, pressing of sheet pile, welding work for preparation of sheetpiling demolition of existing pavilion and felling of tree TA50 at Victoria Park Zone 13 were conducted at the concerned location during the time of complaint. Based on information and photo record provided by the RSS, dust mitigation measures including water spraying during dust generating works were implemented by the Contractor at the concerned location on 24 Dec 2013. Follow-up investigation was conducted on 27 Dec 2013 during weekly environmental inspection, dust mitigation measures including water and major dust generation works were confirmed in place despite a general reminder was given to the contractor to enhance the water spraying to dusty haul road during dry season. Based on on-going site inspection and the follow-up investigation, the site condition was considered generally satisfactory and no non-conformance was identified. Upon further review on the supplementary information provided by the complainant on 31 Dec 2013 and investigation conducted on 2 Ja 2014, the tree felling work of tree TA50 was located nearest to the location of the complainant. According to the location plan provided by the RSS and on site investigation, the tree	Case closed and full investigation report issued on 3 Jan 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					for TA50 was immediately in front of the location of the complainant. Based on site observation, scrap material of bark and leaves inevitably generated from cutting of branches during tree felling work was considered to be the most probable cause for the observation raised by the complainant at the concerned location on 24 Dec 2013. Furthermore, welding work was observed near the concerned location and was considered to be the potential source for the smell and exhaust fumes as described by the complainant. Notwithstanding the above, welding work was not identified as a work activity with air quality impact under Project EIA report but it would be desirable to implement preventive measures to minimize potential nuisance to nearby public.	
140123	22 Jan 2014	ICC Case Ref.:1- 494077682	Causeway Bay Typhoon Shelter	Construction works have been undertaken during restricted hours until 2300 hrs and occasionally the working hours were extended to around 0100 hrs at nighttime period over the last two to three months at a construction site located within Causeway Bay Typhoon Shelter. For instance, concreting and excavation works were conducted at the concerned location on 22 Jan 2014 during nighttime hours and generated noise impact to the complainant.	ET confirmed with the Resident Site Staff that No construction activity was undertaken at workzone TS1 under HY/2009/15 within Causeway Bay Typhoon Shelter after 1900 hrs on 21 Jan 2014. No construction activity was undertaken at workzone TS3 under HY/2010/08 within Causeway Bay Typhoon Shelter after 1900 hrs on 21 Jan 2014. Concreting for base slab and hanger wall was conducted at workzone TS2 under HY/2009/15 within Causeway Bay Typhoon Shelter from 1900 to 0000 hrs on 21 Jan 2014; Total 8 no.s of concrete lorry mixers, 1 no. of water pump, 2 no.s of concrete pumps (lorry mounted), 1 no .of mobile crane QPME (diesel) and 3 no.s of vibratory pokers were operating from 1900 to 0000hrs on 21 Jan 2014. Concreting for base slab and hanger wall was conducted at workzone TS2 under HY/2009/15 within Causeway Bay Typhoon Shelter from 0000 to 0700 hrs on 22 Jan 2014; Total 1. no of concrete lorry mixer, 1 no. of water pump, 1 no. of concrete pump (lorry mounted), 1 no. of vibratory poker were operating from 1900 to 0000hrs on 22 Jan 2014;	Case closed and full investigation report issued on 4 Feb 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					 According to the relevant site records, from 1900-0000hrs on 21 Jan 2014, concreting for base slab and hanger wall was conducted at workzone TS2 under HY/2009/15 within Causeway Bay Typhoon Shelter. Total 8 no.s of concrete pumps (lorry mounted), 1 no. of mobile crane QPME (diesel) and 3 no.s of vibratory pokers were operating at the above period. From 0000 to 0700 hrs on 22 Jan 2014, concreting for base slab and hanger wall was conducted at workzone TS2 under HY/2009/15 within Causeway Bay Typhoon Shelter. Total 1. no of concrete lorry mixer, 1 no. of water pump, 1 no. of concrete pump (lorry mounted), 1 no. of water pump, 1 no. of concrete pump (lorry mounted), 1 no. of vibratory poker were found operating at the above period. After reviewing relevant photo records and information verified by RSS and the Construction Noise Permit (CNP) no.GW-RS1384-13, it was considered that several conditions of CNP GW-RS1384-13 were not fulfilled by the Contractor in particular for the item(s) below, No acoustic installation was provided for the relevant PME(s) used as stated in CNP conditon 3.d.during the concerned concreting works. From 1900 to 2300 hours on 21 Jan 2014, the PME(s) used on-site did not comply with any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in CNP no.GW-RS1384-13. From 1900 to 2300 hours on 21 Jan 2014, the PME(s) used by the Contractor on-site did not comply with any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in CNP no.GW-RS1384-13. From 1900 to 2300 hours on 21 Jan 2014, the PME(s) used by the Contractor on-site did not comply with any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in CNP no.GW-RS1384-13. From 1900 to 2300 hours on 21 Jan 2014, the PME(s) used by the Contractor on-site did not comply with any given PME grouping requirement(s) as stated in CNP no.GW-RS1384-13. From 1900 to 2300 hours on 21 Jan 201	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
140127	24 Jan 2014	ICC Case Ref.: 1-494612639	Works area adjacent to the Victoria Park Bowling Green	Noise generated from piling works conducted at the works area adjacent to the Victoria Park Bowling Green have created nuisance to the Bowling Green users.	ET confirmed with the Resident Site Staff that The major construction activities around the concerned location conducted on 23 Jan 2014 include: Pressing of sheetpile Ch.279-285 (RHS) and Ch.317 for ELS works on 23 Jan 2014. Splicing of sheetpile Ch.275-285 (LHS) for ELS works on 23 Jan 2014. Mitigation measures implemented by the Contractor for the above construction works include: Installation of acoustic panels along hoarding line at East Bowling Green; Installation of addition noise barriers on top of hoarding at East Bowling Green; Display of publicity notices along hoarding line; and No noisy work shall be carried out at the areas adjoining East Bowling Green as if there is any Bowling Green competition event to be held (i.e. Saturday afternoon). According to relevant site records, pressing of sheetpile Ch.279-285 (RHS) and Ch.317 for ELS works and splicing of sheetpile Ch.275-285 (LHS) for ELS works were conducted at the concerned location during the time of complaint. Based on the photo records and information verified by RSS, noise mitigation measures including installation of acoustic panels along hoarding line at East Bowling Green and installation of addition noise barriers on top of hoarding ta East Bowling Green measures including installation of acoustic panels along hoarding line at East Bowling Green measures including installation of acoustic panels along hoarding the tast Bowling Green were implemented by the Contractor at the concerned location. Furthermore, no noisy work was conducted by contractor at the areas adjoining	Case closed and full investigation report issued on 6 Feb 2014.



	Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					East Bowling Green when there is any Bowling Green competition event to be held.	
					Follow-up investigation was conducted on 29 Jan 2014 during weekly environmental inspection, noise mitigation measures including noise barriers and acoustic panels were confirmed in place and maintained in good condition. According to previous environmental inspections recorded in Jan 2014, no particular observation regarding the noise impact was recorded. As such, no non- conformity was identified.	
140311	27 Feb 2014	EPD Complaint Case (Ref:H04/RS/00 04232-14) received by ET on 11 March 2014	Central IFC Area	Excessive noise (from the operation of compressors, other heavy machinery and concrete breaking) was emanated from the construction site near IFC in daytime on 27 Feb 2014.	ET confirmed with the Resident Site Staff that The major construction activities at the concerned location conducted on 27 Feb 2014 (Daytime) include: Backfilling works between north wall and sheetpiles and for roof slab; Site hoarding removal; Formwork erection and removal works, falsework erection; Concrete breaking works at roof slab and base slab and breaking up of existing tunnel corner; Concreting works for profile barrier inside cut and cover tunnel; and Rebar fixing works and WVB basement remediation works. Mitigation measures implemented by the Contractor for the above construction works include: Use of quiet plants (air compressor with a	Interim report submitted to EPD on 18 March 2014, EPD advised no further comment on 26 March 2014 and final report for case closing issued on 26 March 2014



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to relevant site records, major noise emanating construction activities conducted around the concerned location on 27 Feb 2014 include concrete breaking works at roof slab and base slab and breaking up of existing tunnel corner and concreting works.	
					Based on information verified by the RSS, noise mitigation measure including utilization of quiet air compressor with noise emission label of 99 dB(A) was implemented by the Contractor on the 27 February 2014 to minimize the potential noise impact.	
					Having reviewed the monitoring data of the monitoring stations in the vicinity of the construction site near IFC, namely noise monitoring stations M7e and M7w, no limit level exceedances were recorded on 24 Feb 2014 and 4 March 2014 and the major concrete breaking works at the concerned location conducted on 27 February 2014 was continued across the above monitoring period. In addition, no particular observations regarding noise impact were recorded during weekly site inspection conducted on 27 Feb 2014. No non-conformity was identified. As such, the construction activities under Contract HY/2009/18 were considered generally in compliance with the statutory requirement. Nevertheless, in view of the concern regarding noise nuisance raised by public, it is considered desirable for the Contractor to review and strengthen the noise mitigation measures around	
					the concerned location. Follow-up inspection was conducted during weekly environmental inspection on 13 March 2014, additional noise mitigation measure including erection of noise blanket for concrete breaking works were implemented by the Contractor to further minimize the noise nuisance to nearby public	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
140623	11 June 2014	EPD Complaint Case (Ref:H04/RS/00 013590-14) received by ET on 23 June 2014	Foot Bridge to Central Pier 7	Excessive Paint Spray Odour	A public complaint regarding odour concern referred by EPD was received by ET on 23 June 2014. The complainant reported that excessive paint spray odour was detected at the foot-bridge to the Central Pier 7. ET confirmed with the Resident Site Staff that spraying of waterproofing membrane (integritank) from Ch1700 to Ch1705 was conducted at roof slab Bay12 on 11 June 2014 and Screeding concrete placing from Ch1700 to Ch1683 was conducted at roof slab Bay12 on 11 June 2014 and Backfilling and removal of concrete blocks was conducted at roof slab Bay 11 and Bay 10-north on 11 June 2014 According to relevant site records, major construction activities conducted around the concerned location on 11 June 2014 include spraying of waterproofing membrane (integritank) from Ch1700 to Ch1705; screeding concrete placing from Ch1700 to Ch1683 and backfilling and removal of concrete blocks. Having reviewed the relevant information verified by RSS, the chemicals applied at the concerned area on 11 June 2014 are waterproof paint and paint adhesives. In view of the concern regarding odour nuisance raised by the public, it is considered desirable for the Contractor to review the application method for waterproof layer nearby public area to minimize the nuisance caused to the surroundings.	Preliminary report issued on 25 June 2014. Interim report submitted to EPD on 30 June 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up inspection was conducted during weekly environmental inspection on 26 June 2014, no further spraying works was conducted by the Contractor at the concerned area and no particular odour was observed at the concerned location.	
20140723	21 July 2014	ICC complaint (ICC Case Ref.: 2-341537112) received by ET on 23 July 2014	Area opposite to Ngan Tao Building	Noise nuisance due to works and machine at opposite project site during nighttime	A public complaint regarding construction noise impact referred by RSS was received by ET on 25 July 2014 (ICC Case Ref.: 2-341537112 dated 21 July 2014). The complainant reported that : At 00:57hrs on 21 July 2014, he could not sleep due to work and machine at the project site opposite to the building (Ngan Tao Building), where he was living, were still going on and in operation. Noise traveled to his flat despite it was some distance away. ET confirmed with the Resident Site Staff that dewatering works was conducted under HY/2009/19 at the works area at Watson Road from around 23:00hrs on 20 July 2014 to 01:00hrs on 21 July 2014. Total 1 no. of generator and 23 nos. of dewatering pumps were in operation. Mobilization of telescopic arm excavator to trailer truck was performed under HY/2009/19 at the works area at Watson Road from around 00:15hrs to 01:00hrs on 21 July 2014. Total 1 no. of telescopic arm excavator and 1 no. of trailer truck were in operation. According to the relevant site records under Contract HY/2009/19, from around 23:00hrs on 20 July 2014 to 01:00hrs on 21 July 2014, dewatering works was conducted under HY/2009/19 at the works area at Watson Road. Total 1 no. of generator and 23 nos. of dewatering pump were in	Final Investigation report (Issue1) issued on 31 July 2014. Final investigation report (Issue 2) based on further follow- up issued on 12 Aug 2014.



operation at the above period. In addition, mobilization of telescopic arm excavator to trailer truck was performed under HY/2009/19 at the works area at Watson Road from around 00:15hrs to 01:00hrs on 21 July 2014. Total 1 no. of telescopic arm excavator and 1 no. of trailer truck were in operation. After reviewing relevant records and information verified by RSS and the Construction Noise Permit	Complaint Date o Log No. Compla		Location of Complainant	Nature of Complaint	Outcome	Status
the below condition of CNP no.GW-RS0152-14 was not fulfilled by the Contractor of HY/2009/19. From 00:15hrs to 01:00hrs on 21 July 2014, the PME(s) (1 no. of telescopic arm excavator and 1 no. of trailer truck) operated under the Contractor of HY/2009/19 on-site could not follow any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in no.GW- RS0152-14. Notwithstanding the above, according to the information provided by the RSS, the telescopic arm excavator was mobilized at night time hours with consideration that passage of vehicle with large plant & machinery through cross harbour tunnel shall be conducted after mid-night. the Contractor of HY/2009/19 was advised to review the need to renew relevant CNP for PME grouping with respect to specific site operation requirements such that the Construction Noise Permit would be followed. Furthermore, the Contractor of HY/2009/19 was suggested to review the arrangement for PME mobilization with maintenance need to be conducted within specific	Log No. Compla	int and Received By	Complainant		 In addition, mobilization of telescopic arm excavator to trailer truck was performed under HY/2009/19 at the works area at Watson Road from around 00:15hrs to 01:00hrs on 21 July 2014. Total 1 no. of telescopic arm excavator and 1 no. of trailer truck were in operation. After reviewing relevant records and information verified by RSS and the Construction Noise Permit (CNP) no. GW-RS0152-14, it was considered that the below condition of CNP no.GW-RS0152-14 was not fulfilled by the Contractor of HY/2009/19. From 00:15hrs to 01:00hrs on 21 July 2014, the PME(s) (1 no. of telescopic arm excavator and 1 no. of trailer truck) operated under the Contractor of HY/2009/19 on-site could not follow any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in no.GW-RS0152-14. Notwithstanding the above, according to the information provided by the RSS, the telescopic arm excavator was mobilized at night time hours with consideration that passage of vehicle with large plant & machinery through cross harbour tunnel shall be conducted after mid-night. the Contractor of HY/2009/19 was advised to review the need to renew relevant CNP for PME grouping with respect to specific site operation requirements such that the Construction Noise Permit would be followed. Furthermore, the Contractor of HY/2009/19 was suggested to review the arrangement for PME mobilization with 	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Noise of sand and gravel movements at area opposite to the Harbour Heights	A public complaint regarding construction noise impact referred by RSS was received by ET on 01 Aug 2014 (ICC Case Ref.: 2-360638977 dated 31 July 2014). The complainant reported that at 01:20hrs on 30 July 2014, the complainant was woken up by the noise of sand and gravel movements at area opposite to the Harbour Heights. ET confirmed with the Resident Site Staff that EVB excavation was undertaken at the works area around Watson Road under HY/2009/19 before 23:00hrs on 29 July 2014. (Total 1 no. of excavator,1 no. of dump truck, 23 nos. of underground dewatering pump and 3 nos. of generator were in operation). Dewatering works was undertaken at works area around Watson Road under HY/2009/19 from 23:00hrs on 29 July 2104 to 01:00 hrs on 30 July 2014. (Total 23 nos. of underground dewatering	Status Final investigation report issued on 12 Aug 2014.
					pumps and 1 no. of generator were in operation). Mobilization of PMEs was performed at works area around Watson Road under HY/2009/19 from 00:45hrs to 01:30hrs on 30 July 2014. (1 no. of excavation machine and 1 no. of dump truck were in operation). No other construction activity or operation was performed at the area opposite to Harbour Heights from 23:00hrs on 29 July 2014 to 01:00hrs on 30 July 2014 under HY/2009/19. According to the relevant site records, before 2300hrs on 29 July 2014, EVB excavation at the works area around Watson Road was conducted under HY/2009/19. (Total 1 no. of dump truck , 1 no. of excavator, 3 nos. of generators and 23 nos. of dewatering pumps were in operation at the	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					above period). From around 23:00hrs on 29 July 2014 to 01:00hrs on 30 July 2014, dewatering works at works area around Watson Road was conducted under HY/2009/19. Total 23 nos. of dewatering pumps were operating at the above period.	
					In addition, mobilization of PMEs was performed at works area around Watson Road under HY/2009/19 from 00:45hrs to 01:30hrs on 30 July 2014. Total 1 no. of excavation machine and 1 no. of dump truck were in operation.After reviewing relevant records and information verified by RSS and the Construction Noise Permit (CNP) no.GW- RS0152-14, it was considered the below condition of CNP GW-RS0152-14 was not fulfilled by the Contractor of HY/2009/19. From around 00:45hrs to 01:30hrs on 30 July 2014, the operation of PME(s) (1 no. of excavator and 1 no. of dump truck) under the Contractor of HY/2009/19 on-site could not follow any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in no.GW-RS0152-14.	
					Notwithstanding the above, according to the information provided by the RSS, the excavator and dump truck were mobilized away from the edge of the temporary ELS structure towards the area opposite to the Harbour Heights after 23:00hrs under safety consideration. The Contractor of HY/2009/19 was advised to review the arrangement and location for retaining and securing PME(s)/ plants to minimize the movements of PME or plants after completion of works such that the Construction Noise Permit would be followed.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20140929	26 Sep 2014	ICC complaint (ICC Case Ref.: 2- 466911619) received by ET on 29 September 2014	IEC flyover opposite to City Garden	Light originating from the flyover under Central- WanChai Bypass Project was emitted towards City Garden direction and caused light nuisance	A public complaint regarding visual impact referred by RSS was received by ET on 29 September 2014 (ICC Case Ref.: 2-466911619 dated 26 September 2014) The complainant reported that on 26 September 2014 at around 00:50hrs, light originating from the flyover under Central-WanChai Bypass Project was emitted towards City Garden direction and caused light nuisance. ET confirmed with the Resident Site Staff that the light emission on 25 and 26 September 2014 at the concerned area was originated from the temporary lighting provided at the soffit of the permanent noise enclosure at the new Island Eastern Corridor (IEC) Eastbound which was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after the traffic diversion on 28 September 2014. According to the relevant information provided by RSS, the light emission on 25 and 26 September 2014 at the concerned location was originated from the temporary lighting provided at the sofit of the permanent noise enclosure at the new Islannd Eastern Corridor Eastbound. The lighting was necessary to provide sufficient illumination for the traffic diversion on 28 September 2014. Nevertheless, in view of the public concern regarding light nuisance raised by the public, it is considered desirable for the Contractor to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surrounding receivers as far as practicable.	Final Investigation report submitted on 9 October 2014.



Follow-up inspection was conducted during weekly environmental inspection on 8 October 2014, additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings. Further to the interim measure implemented by the Contractor of HY/2009/19, the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings. The Contractor of HY/2009/19 was suggested to review the lighting arrangement and implement additional measures to minimize the private to minimize the private additional measures to minimize the private to minimize the private additional measures to minimize the private to minimize t	Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
Additional measures to this stress of minimize the hubsarde caused to the surroundings receivers as far as practicable. Additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings and the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings.						 environmental inspection on 8 October 2014, additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings. Further to the interim measure implemented by the Contractor of HY/2009/19, the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings. The Contractor of HY/2009/19 was suggested to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surroundings receivers as far as practicable. Additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings and the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the surroundings and the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light 	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20141006	25,26 Sep 2014	ICC complaint (ICC Case Ref.: 2-469099657) received by ET on 06 October 2014	IEC flyover opposite to City Garden	Light originating from the flyover under Central- WanChai Bypass Project was emitted towards City Garden direction and caused light nuisance	A public complaint regarding visual impact referred by RSS was received by ET on 6 October 2014 (ICC Case Ref.: 2-469099657 dated 26 September 2014). The complainant reported that on 25 September 2014 at around 23:23 hrs, light originating from the flyover under Central-Wan Chai Bypass Project was emitted towards City Garden direction and caused light nuisance. ET confirmed with the Resident Site Staff that the light emission on 25 and 26 September 2014 at the concerned area was originated from the temporary lighting provided at the soffit of the permanent noise enclosure at the new Island Eastern Corridor (IEC) Eastbound which was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after the traffic diversion on 28 September 2014. According to the relevant information provided by RSS, the light emission on 25 and 26 September 2014 at the concerned location was originated from the temporary lighting provided at the sofit of the permanent noise enclosure at the new Islannd Eastern Corridor Eastbound. The lighting was necessary to provide sufficient illumination for the traffic diversion on 28 September 2014 at the concerned location was originated from the temporary lighting provided at the sofit of the permanent noise enclosure at the new Islannd Eastern Corridor Eastbound.	Final Investigation report submitted on 9 October 2014.



Follow-up inspection was conducted during weekly environmental inspection on 8 October 2014, additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings. Further to the interim measure implemented by the Contractor of HY/2009/19, the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings. The Contractor of HY/2009/19 was suggested to review the lighting arrangement and implement	Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
additional measures to minimize the nuisance caused to the surroundings receivers as far as practicable. Additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings and the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings.						 environmental inspection on 8 October 2014, additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings. Further to the interim measure implemented by the Contractor of HY/2009/19, the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings. The Contractor of HY/2009/19 was suggested to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surroundings receivers as far as practicable. Additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings and the Contractor of HY/2009/19 will replace the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light 	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20141010	07 Oct 2014	ICC complaint (ICC Case Ref.: 2-487376144) received by ET on 10 October 2014	IEC flyover opposite to City Garden	Light originating from the flyover under Central- WanChai Bypass Project was emitted towards City Garden direction and caused light nuisance	ET confirmed with the Resident Site Staff that temporary lighting was provided at the concerned area at the soffit of the permanent noise enclosure at the new Island Eastern Corridor (IEC) Eastbound which was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after the traffic diversion on 28 September 2014. Temporary lighting was provided at the concerned area at the soffit of the permanent noise enclosure at the new Island Eastern Corridor (IEC) Eastbound which was necessary to provide sufficient illumination for the traffic operation on the new IEC Eastbound after the traffic diversion on 28 September 2014. In view of the public concern regarding light nuisance raised by the public, it is considered desirable for the Contractor to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surrounding receivers as far as practicable. During weekly environmental inspection on 8 October 2014, additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure to minimize the nuisance cased to the surroundings. Further to the interim measure implemented, on 13 October 2014 the Contractor of HY/2009/19 have replaced the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings.	Final investigation report submitted on 14 Oct 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					The Contractor of HY/2009/19 was suggested to review the lighting arrangement and implement additional measures to minimize the nuisance caused to the surroundings receivers as far as practicable. Additional measures including erection of green net and tarpaulin sheet were provided by the Contractor of HY/2009/19 at the concerned area as interim measure and on 13 October 2014 the Contractor of HY/2009/19 have replaced the concerned temporary lighting with temporary lighting facing Victoria Harbour at the other side of the road to minimize the light nuisance to the surroundings.	
141016	14 Oct 2014	EPD complaint EPD Ref.:H05/RS/00 025795-14) received by ET on 16 October 2014	work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	Construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	A public complaint regarding construction noise impact referred by EPD was received by ET on 16 October 2014 (EPD Ref.: EP860/E2/24 Annex IV dated 16 October 2014). The complainant reported that construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground. ET confirmed with the Resident Site Staff that From 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.	Updated interim investigation with supplementar y information submitted to EPD on 17 November 2014. EPD advised no further comment on the updated interim report and case closed on 27 Nov 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.	
					Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.	
					From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway.	
					Total one scissor platform and two hand held drills (battery) were in operation.	
					From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road.Total one crane lorry was in operation.	
					According to the relevant site records under Contract HK/2009/02, from 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.	
					From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					 From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway. Total one scissor platform and two hand held drills (battery) were in operation. From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road. Total one crane lorry was in operation. In view of the above findings, no direct information associated with the noise concern was considered available. 	
20141108	07 Nov 2014	EPD complaint (EPD Ref.: H05/RS/00027 815-14) received by ET on 10 November 2014	Construction site at old Wan Chai Ferry Pier	Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool.	A public complaint regarding odour concern referred by EPD was received by ET on 07 November 2014 (EPD Ref.: H05/RS/00027815-14 dated 10 November 2014). The complainant reported that Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool. ET confirmed with the Resident Site Staff that ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool). Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated. Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.	Interim investigation report submitted to EPD on 17 November 2014. EPD advised no comment on the interim report and case closed on 1 Dec 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Dredging works was conducted on 7 November 2014 during daytime at WCR3 (East of old Wan Chai Ferry Pier)	
					Total 1 no .of dredger, 1 no. of hopper and 1 no. of tug boat were operated.	
					According to the relevant site records under Contract HK/2009/02, ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool). Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated. Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.	
					Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site. The condition of chemical waste storage was considered satisfactory and no malodour was identified. Despite no information related to malodour was identified, the Contractor was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.	
					Based on the relevant information provided by RSS, despite no information associated with the malodour concern was identified after investigation, the Contractor was reminded to conduct regular checking on the condition of PME used on site to ensure only well maintained PME are used on site	
					The interim report would be submitted to EPD on 17 November 2014.	



excavators, 1 no. of derrick barge and 1 no. tug boat were operated. According to the relevant site records under Contract HK/2009/02, demolition works was conducted on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated. In addition, investigation found that due to malfunctioning of one of the excavators deployed at old Wan Chai Ferry Pier, dark smoke was emitted from the defective excavator for a short period of approximately 30 seconds at around 15:00 hrs on 12 November 2014. The operation of excavator was immediately suspended and followed by repair works. The normal operation of	Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
the excavator was resumed after repair. Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site and the Contractor of HK/2009/02 was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.		12 Nov	EPD complaint (EPD Ref.: H05/RS/00028 253-14) received by ET on 13 November	Construction site at old Wan Chai Ferry	emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that	referred by EPD was received by ET on 13 November 2014 (EPD Ref.: H05/RS/00028253-14 dated 13 November 2014). The complainant reported thatMalodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians. (Contract HK/2009/02) ET confirmed with the Resident Site Staff that demolition works was conducted under Contract HK/2009/02 on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated. According to the relevant site records under Contract HK/2009/02, demolition works was conducted on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated. In addition, investigation found that due to malfunctioning of one of the excavators deployed at old Wan Chai Ferry Pier, dark smoke was emitted from the defective excavator for a short period of approximately 30 seconds at around 15:00 hrs on 12 November 2014. The operation of excavator was immediately suspended and followed by repair works. The normal operation of the excavator was resumed after repair. Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site and the Contractor of HK/2009/02 was reminded to conduct regular checking on the condition of PMEs to ensure only	investigation report submitted to EPD on 19 November 2014. EPD advised no comment on the interim report and case closed on 8



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20150127	21 Jan 2015	EPD complaint (EPD Ref.: H05/RS/00001 725-15) received by ET on 27 January 2015 and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015	A portion of Hung Hing Road immediately to the east of Marsh Road near SPCA	Construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public.	A public complaint regarding air quality impact referred by EPD was received by ET on 27 January 2015 (EPD Case Ref.: H05/RS/00001725-15 dated 27 January 2015) and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015. The complainant reported that construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public. ET confirmed with the Resident Site Staff that the major construction activities around the concerned location conducted on 21 January 2015 include breaking of seawall blocks and D-wall at TPCWAW; concreting, grouting and drilling works at TPCWAW;reclamation/ backfilling works at TPCWAW Mitigation measures implemented by the Contractor for the above construction works include spraying haul road with water; covering bagged cement with tarpaulin; providing three sided and top covering for grouting stations; providing water spraying to dusty activities such as breaking works According to the relevant site records, breaking of seawall blocks and D-wall, concreting, grouting and drilling works and reclamation/ backfilling works were conducted at TPCWAW. Dust mitigation measures including spraying haul road with water, covering bagged cement with tarpaulin, providing three sided and top covering for grouting stations and water spraying to dusty activities such as breaking works were implemented by the Contractor of HY/2009/15 near the concerned location on 21 January 2015.	Interim report submitted to EPD on 9 February 2015, EPD advised no comment on 27 February 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up investigation was conducted on 27 January 2015 during weekly environmental inspection, dust mitigation measures including water spraying for dusty haul road and major dust generation works; and provision of three sides and top covering for grouting station were confirmed in place.	
					In addition, based on the review of the monitoring data of the monitoring station located at the concerned location raised by the complainant, namely monitoring station CMA3a, no action or limit level exceedance was recorded during air quality monitoring conducted on 20 and 21 January 2015. Nevertheless, the Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on the complaint date was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants.	
					As such, the site condition under Contract HY/2009/15 at the concerned location was considered to be generally satisfactory and no non- conformity related to cumulative air quality impact was observed. Nevertheless, in view of the public concern, the contractor was reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.	
					ET confirmed with the Resident Site Staff that the major construction activities under Contract HK/2009/02 around the concerned location conducted on 21 January 2015 include trenching grabbing for D-wall construction at temporary road eastward, shear pin installation at temporary road westward and ground Investigation drilling at temporary road westward	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Mitigation measures implemented by the Contractor of HK/2009/02 for the above construction works include regular water spraying at haul road, vehicle wheel-washing at the ingress/egress (Gate No. 4) to the temporary road northward and frequent water spraying at the ingress/egress (Gate No. 4) to the temporary road. According to the relevant site records, trenching grabbing for D-wall construction, shear pin installation and ground investigation drilling works were conducted at the concerned location. Dust mitigation measures including water spraying for haul road, vehicle wheel washing and hard paving for a section of works area nearby public road were implemented by the Contractor of HK/2009/02 near the concerned location on 21 January 2015. Follow-up investigation was conducted on 5 February 2015 during weekly environmental inspection, dust mitigation measures including water spraying for dusty haul road and major dust generation works and provision of wheel washing combine with cleaning of public road were confirmed in place and no dust related impact from the construction works was observed. The Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on 21 January 2015 was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants. Based on reviewing relevant impact monitoring data, elevated TSP were recorded at monitoring stations across Wan Chai West area to North Point area and a non-Project related exceedance was recorded at nearby monitoring station CMA4a (at SPCA) on 21 January 2015 due to ambient air pollutant.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					In addition. it was noted that a section of the works area at the concerned location was not provided with site hoarding. Based on further review on relevant records it was noted that the works area at concerned section was either hard paved or have to maintain adequate line of sight due to traffic safety consideration. The Contractor of HK/2009/02 was advised to inform EPD with respect to the site constraint and provide relevant updated meeting records on the arrangement for review.	
					In view of the public concern, the contractor has committed to conduct additional cleaning of the concerned public road section once a week to minimize potential nuisance caused to nearby road users. The contractor was also reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.	
20150409	07 April 2015 09 April 2015	EPD complaint (Ref.:H05/RS/ 00008074-15 dated 9 April 2015) received by ET on 09 April 2015	Construction site exit near Expo Drive Central; Construction site gate V2 & gate V8	Construction dust was generated from lorries transporting out of the construction via site exit without wheel washing	A public complaint regarding construction dust impact referred by EPD was received by ET on 09 April 2015 (EPD Ref.:H05/RS/00008074-15 dated 9 April 2015). The complainant reported that: Construction dust was generated from lorries transporting out of the construction via site exit near Expo Drive Central without wheel washing at the morning of 7 April 2015. Lorries were also found transporting out of the construction site via gates V2 and V8 without wheel washing and causing dust nuisance at about 10:30 hours on 9 April 2015.	Interim report submitted to EPD on 17 April 2015, EPD advised no comment on 30 April 2015 on the interim report submitted and case closed.
					ET confirmed with the Resident Site Staff that on 7 April 2015, major vehicle movements included oil tanker passing at Gate V2 at Expo Drive East and dump truck passing at Gate V8 at Expo Drive Central under Contract HK/2009/01.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					2. On 9 April 2015. major vehicle movements include oil tanker, crane lorry and dump truck passing at at Gate V2 at Expo Drive East and dump truck at Gate V8 at Expo Drive Central under Contract HK/2009/01.	
					Mitigation measures adopted by the Contractor of HK/2009/01 at the above locations include water hose was provided for wheel washing at Gate V2 and Gate V8, concrete paving at site exit, dump truck fitted with mechanic cover and cleaned before leaving construction site, regular street washing at Expo Drive Central.	
					According to the relevant site records under Contract HK/2009/01, on 7 April 2015, major vehicle movements included oil tanker passing at Gate V2 at Expo Drive East and dump truck passing at Gate V8 at Expo Drive Central under Contract HK/2009/01 while on 9 April 2015 major vechicle movements include oil tanker, crane lorry and dump truck passing at at Gate V2 at Expo Drive East and dump truck at Gate V8 at Expo Drive Central under Contract HK/2009/01.	
					At the above locations, mitigation measures including water hose for wheel washing at Gate V2 and Gate V8; concrete paving at site exit; dump truck fitted with mechanic cover and cleaned before leaving construction site and regular street washing at Expo Drive Central were generally adopted by the Contractor of HK/2009/01.	
					In view of the public concern on the complaint date, the Contractor of HK/2009/01 was advised to conduct cleaning at the concerned site exit point and the section of public road adjoining the site exit to clear any residue grit and silt desposit to avoid further dust impact.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow up inspection was conducted on 16 April 2015 during weekly environmental inspection and mitigation measures including water spraying for dusty haul road and provision of wheel washing were in place. The construction site exit was observed clear from residue silt / grit at the concerned location.	
					In view of the public concern, the contractor was advised to conduct training to the construction site workers to enhance the effectiveness of wheel washing and to ensure proper wheel washing is provided for dump truck and other vehicle prior to leaving the construction site to avoid generating any dust nuisance.	
20150409A	03 April 2015 to 07 April 2015	EPD complaint (Ref.:H05/RS/ 00007861-15 dated 9 April 2015) received by ET on 09 April 2015	Construction site at Convention Avenue near Renaissance Harbour View Hotel	Construction noise was emanated from the construction site at Convention Avenue near Renaissance Habour View Hotel during the period of Easter Holiday	A public complaint regarding construction noise impact referred by EPD was received by ET on 09 April 2015 (EPD Ref.:H05/RS/00007861-15 dated 9 April 2015). The complainant reported that construction noise was emanated from the construction site at Convention Avenue near Renaissance Habour View Hotel during the period of Easter Holiday, including April 3 at about 13:00 hours. ET confirmed with the Resident Site Staff that from 3 April 2015 to 7 April 2015, from 08:00 hours to 18:00 hours, and at about 13:00 hours on 3 April 2015 at area CWB Tunnel Stage 3, backfilling works was conducted under HK/2009/01. Either 1 no. of dump truck and 1. no. of excavator was operated on site at each given time during the concerned period. According to the relevant site records under Contract HK/2009/01, from across 08:00hrs to 18:00hrs during the period from 3 April 2015 to 7	Interim report submitted to EPD on 17 April 2015, EPD advised no comment on 30 April 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					concerned period and the relevant Construction Noise Permit GW-RS0104-15 for the works was in place and the same construction activity was undertaken at around 13:00hrs on 3 April 2015. No other concurrent construction activity was undertaken at the concerned location during the concerned period under Contract HK/2009/01. The construction activity conducted under Contract HK/2009/01 during the concerned period was in compliance with the statutory requirement. Nevertheless, in view of the concern regarding the noise nuisance raised by the public at the concerned location, it is considered desirable for the Contractor of HK/2009/01 to review the truck unloading procedures of the specific construction	
20150415	13 April	ICC complaint	Construction Site at	Unnecssary light nuisance	task to minimize potential noise emanated during the course for work. A public complaint regarding visual impact received	Final
	2015	case (ICC Case Ref.: 2- 885677297 dated 13 April 2015) recevied by ET on 15 April 2015	Causeway Bay Typhoon Bay Shelter	from the construction site	by the RSS was referred to the ET on 15 April 2015 (ICC Case Ref.: 2-885677297 dated 13 April 2015). The complainant reported that " I live in a building next to Gloucester Road in Causeway Bay. Recently, I am suffering from unnecessary light source from the construction site. The banners of the construction companies are always illuminated with very bright lights."	Investigation report issued on 20 April 2015 and case closed
					ET confirmed with the Resident Site Staff that the concerned lighting for the banners was maintained under Contract HY/2010/08.	
					The concerned lighting for the banners was maintained under Contract HY/2010/08 and the concerned lighting was subsequently switched off at all times since 13 April 2015 to alleviate the lighting nuisance caused to the surroundings.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20150423	21 April 2015	EPD complaint case (EPD Case Ref: :H05/RS/ 00009456-15 dated 23 April 2015) recevied by ET on 23 April 2015	Road work at Fleming Road and Convention Avenue near Renaissance Harbour View Hotel	Construction noise emanated from the road work at Fleming Road and Convention Avenue near Renaissance Harbour View Hotel causing nuisance	A public complaint regarding construction noise impact referred by EPD was received by ET on 23 April 2015 (EPD Ref.:H05/RS/00009456-15 dated 23 April 2015). The complainant reported that construction noise emanated from the road work at Fleming Road and Convention Avenue near Renaissance Harbour View Hotel almost every night recently causing nuisance. ET confirmed with the Resident Site Staff that from 21:00hrs on 20 April 2015 to 06:00hrs on 21 April 2015 and from 21:00hrs on 21 April 2015 to 06:00hrs on 22 April 2015, cooling main connection works was undertaken by the Contractor of Contract HK/2009/01 at the concerned location. Total 1 no. of crane lorry and 1 no. of excavator were in operation. According to the relevant site records under Contract HK/2009/01, from 21:00hrs on 20 April 2015 to 06:00hrs on 21 April 2015 and from 21:00hrs on 21 April 2015 to 06:00hrs on 22 April 2015, cooling main connection works was undertaken by the Contractor of Contract HK/2009/01 at the concerned location. Total 1 no. of crane lorry and 1 no. of excavator were in operation during the concerned period and the relevant Construction Noise Permit GW-RS0269-15 was confirmed in place. The construction activity conducted under Contract HK/2009/01 during the concerned period was in compliance with the statutory requirement. In view of the potential noise nuisance, a notice to affected parties was issued by the Contractor of Contract HK/2009/01 to the nearby residents including Renaissance Harbour View Hotel on 17 April 2015. Besides, construction works undertaken by other parties at the concerned location was observed at the concerned period.	Final Investigation report issued on 18 May 2015 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
20150601	29 May 2015	EPD complaint case (EPD Case Ref: :H05/RS/ 00013254-15 dated 1 June 2015) recevied by ET on 23 April 2015	Construction site gates V2 and V3 near Expo Drive Central	Vehicle with plate no. TG2426 was found leaving the construction site at gate V2 near Expo Drive Central without wheel- washed	A public complaint regarding construction dust impact referred by EPD was received by ET on 01 June 2015 (EPD Ref.:H05/RS/00013254-15 dated 1 June 2015). The complainant reported that vehicle with plate no. TG2426 was found leaving the construction site at gate V2 near Expo Drive Central without wheel-washed at about 10:33hrs on 29 May 2015. The complainant also alleged that water spraying at the gates V2 and V3 near Expo Drive Central was insufficient causing dust nuisance to the public. ET confirmed with the Resident Site Staff that on 29 May 2015, vehicle record indicated that concerned vehicle TG 2426 has entered and exited the construction site via gate V3. Mitigation measures adopted by the Contractor of HK/2009/01 at the above locations include, water hose was provided for wheel washing at Gate V2 and Gate V3. According to the relevant site records under Contract HK/2009/01, vehicle record indicated that concerned vehicle TG 2426 has entered and exited the construction site via gate V3 on 29 May 2015 under Contract HK/2009/01. As confirmed by WDII RSS, the concerned construction site area. Follow up inspection was conducted on 3 June 2015 during weekly environmental inspection and mitigation measures including wheel washing were implemented at construction site area. Follow up inspection was conducted on 3 June 2015 during weekly environmental inspection and mitigation measures including wheel washing were implemented at construction site area. Follow up inspection was conducted on 3 June 2015 during weekly environmental inspection and mitigation measures including wheel washing were implemented at construction site area. Follow up inspection was conducted on 3 June 2015 during weekly environmental inspection and mitigation measures including wheel washing were implemented at construction site via Gate V8 without wheel washing. The Contractor was immediately advised to review and strengthen the control measures for vehicle exits to ensure wheel washing are provided for exiting vehicles.	Interim report submitted to EPD on 08 June 2015, EPD advised no comment on 22 June 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					In view of the public concern and the site observation, the Contractor of HK/2009/01 has implemented enhanced site exit control measures using red string to alert drivers to stop their vehicles for cleaning before leaving the construction site and wheel washing facilities including water hose were implemented at Gate V1 and Gate V10 around the concerned location and the vehicle gate V8 was subsequently closed. In addition, removal of spoil arising from wheel washing around site exit location would be conducted by the Contractor of HK/2009/01 as appropriate to alleviate for potential dust impact at construction site exits.	
20150608	04 June 2015	EPD Ref.:H05/RS/0 0013843-15 dated 8 June 2015	A portion of construction site of Contract HK/2012/08 outside Fleet Arcade	Construction noise was generated from the construction site of Contract HK/2012/08 at location outside Fleet Arcade during restricted hours including Sundays and General Holidays.	 A public complaint regarding construction noise impact referred by EPD was received by ET on 8 June 2015 (EPD Ref.:H05/RS/00013843-15 dated 8 June 2015). The complainant reported that construction noise was generated from the construction site of Contract HK/2012/08 at location outside Fleet Arcade during restricted hours including Sundays and General Holidays. ET confirmed with the Resident Site Staff that from 08:00hrs to 18:00hrs on 31 May 2015 (Sunday), construction work including steel welding was conducted under Contract HK/2012/08 at site portion zone A1 opposite to Fleet Arcade. Total one welding machine was in operation. According to the relevant site records under Contract HK/2012/08, from 08:00hrs to 18:00hrs on 31 May 2015 (Sunday), construction work including steel welding was conducted under Contract HK/2012/08 site portion zone A1 opposite to Fleet Arcade. Total one welding machine was in operation and the relevant Construction Noise Permit GW- RS0296-15 was confirmed in place. The construction activity conducted under Contract 	Interim report submitted to EPD on 16 June 2015 and EPD advised no comment on 20 July 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					 HK/2012/08 during the concerned period was in compliance with the statutory requirement. Ad-hoc inspection was conducted during weekly environmental inspection on 9 June 2015 and it was noted that Construction Noise Permits under Contract HK/2012/08 were posted at site entrance locations for public inspection. In view of the potential noise nuisance, the Contractor was reminded to upkeep the site control system for construction works carrying out at restricted hours and night time for Construction Noise Permit compliance. Besides, other construction sites at the concerned location were observed. Furthermore, a meeting was held on 15 June 2015 between the EPD, Contractor of HK/2012/08, WDII RSS team and the Environmental Team on the public concern and the Contractor of HK/2012/08 has committed to review the re-application for the Construction Noise Permits GW-RS0296-15 on usage of PMEs at a portion of site area outside the Fleet Arcade during public holiday including Sundays to minimize for the 	
150622	18 June 2015	EPD Ref.:H05/RS/0 0015054-15 dated 22 June 2015	A mooring location near shore and at location outside Wan Chai Sports Ground	Dark smoke and malodour emission was observed from a hopper barge moored near shore and other construction plants under operation from the reclamation construction site	potential noise nuisance to nearby public. A public complaint regarding dark smoke and malodour concern referred by EPD was received by ET on 22 June 2015 (EPD Ref.: H05/RS/00015054- 15 dated 22 June 2015). The complainant reported that dark smoke and malodour emission was observed from a hopper barge moored near shore and other construction plants under operation from the reclamation construction site with Contract no. HK/2009/02 at location outside Wan Chai Sports Ground caused air pollution. The complainant alleged that the said situation had been observed for a prolonged period.	Interim report submitted to EPD on 29 June 2015 and EPD advised no comment on 20 July 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					ET confirmed with the Resident Site Staff that reinforced bar fixing and concreting work (on 17 June 2015 only) were conducted at Portion 2 from 15 June 2015 to 19 June 2015. Total 3 nos. of mobile crane were in operation. On 17 June 2015, one no. of concrete pump truck and two nos. of concrete mixer were in operation.Excavation and Lateral Support was conducted at Portions 3 & 4 from 15 June 2015 to 19 June 2015. Total 4 nos. of excavator, 2 nos. of truck and 2 nos. of crawler crane were in operation. In addition, on 15 June 2015, 17 June 2015 and 19 June 2015, 1 no. of derrick barge was moored near Portions 3 & 4 for transportation of the excavated material away from site.	
					According to the relevant site records under Contract HK/2009/02, from 15 June 2015 to 19 June 2015, reinforced bar fixing and concreting work (on 17 June 2015 only) were conducted at Portion 2 and total 3 nos. of mobile crane, one no. of concrete pump truck (on 17 June 2015 only) and two nos. of concrete mixer (on 17 June 2015 only) were in operation; excavation and lateral support was conducted at Portions 3 & 4 and total 4 nos. of excavator, 2 nos. of truck and 2 nos. of crawler crane were in operation. Based on relevant site record, no hopper barge was moored under Contract HK/2009/02 around the concerned location while 1 no. of derrick barge was moored under Contract HK/2009/02 near Portions 3 & 4 for transportation of the excavated material from Portions 3 & 4 away from site on 15 June 2015,17 June 2015 and 19 June 2015 respectively.	
					Follow-up inspection was conducted during weekly environmental inspection on 25 June 2015, no dark smoke and malodour emission was observed from the PMEs operating on-site. A derrick barge was	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					observed moored near Portions 3 & 4 and excavated material was transferred to the derrick barge by the excavators on land without barge operation and no particular dark smoke and malodour emission was observed. Nevertheless, the Contractor was reminded to conduct regular checking on the condition of the derrick barge and other PMEs deployed on site to ensure only well maintained PMEs are used to avoid potential dark smoke and maldour emission affecting nearby public.	
150714	11 July 2015	ICC Complaint (Ref:#2- 1149562777) referred by RSS was received by ET on 14 July 2015	A portion of site area adjacent to Hing Fat Street Site entrance	Direct discharge of muddy effluent into marine waters	A public complaint regarding direct discharge of muddy effluent referred by RSS was received by ET on 14 July 2015 (ICC Ref.: #2-1149562777). The complainant reported that: Muddy effluent was directly discharged into nearby marine waters by Chun Wo worker. Further information was received by ET from RSS on 23 July 2015 and the complaint date was clarified to be 11 July 2015 and the concerned vehicle registration number shall be JV 7319. ET confirmed with the Resident Site Staff that no construction works was undertaken by the Contractors HY/2009/19 and adjacent Central WanChai Bypass Project construction site at the concerned location on 11 July 2015. No construction works was undertaken by the Contractor of HY/2009/19 and adjacent Central WanChai Bypass Project construction site at the concerned location on 11 July 2015. No construction works was undertaken by the Contractor of HY/2009/19 and adjacent Central WanChai Bypass Project construction site at the concerned location on 11 July 2015, no direct discharge connection was further observed on site.	Updated Final investigation report submitted on 27 July 2015.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					No construction works was undertaken by Central WanChai Bypass Project at the concerned location and no sump pit or works area under Central WanChai Bypass Project associated with potential muddy effluent discharge was identified. In addition, a construction area with excavated pit under WSD Contract 12/WSD/10 was noted at the concerned location behind the alleged vehicle responsible for direct discharge of muddy effluent. Based on the further review on the information received on 23 July 2015, the alleged direct discharge was observed originating from the works area under WSD Contract 12/WSD/10 and not	
150723	20 July 2015	EPD Ref.:H05/RS/0 0018040-15	Ex-Wanchai Ferry Pier near 720 & & 722 Bus stop	Malodour from marine sediment	 related to the Central Wan Chai Bypass Project construction works. A public complaint regarding malodour referred by EPD was received by ET on 23 July 2015 (EPD Ref.: H05/RS/00018040-15 dated 23 July 2015). 	Interim report submitted to EPD on 30
		dated 23 July		The complainant reported that malodour from marine sediment was scented at ex-Wanchai ferry pier near route 720 & 722 bus stop. (Contract HK/2009/02).	July 2015. EPD advised no comment on 17 August 2015 on the interim report	
					ET confirmed with the Resident Site Staff that Rockfill placing works was conducted by one derrick barge at the concerned location (WCR3) under Contract HK/2009/02 on 20 July 2015. No marine sediment was stored or placed on site at the concerned location under Contract HK/2009/02 on 20 July 2015.	submitted and case closed.
					According to the relevant site records under Contract HK/2009/02, rockfill placing works was conducted by one derrick barge at WCR3 area on 20 July 2015 and no marine sediment was stored or placed on site at the concerned location on the concerned date.	



Complaint Log No. 0	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up inspection was conducted during weekly environmental inspection on 29 July 2015. No marine sediment was observed stored or placed at the concerned location while it was noted that a culvert outfall with potential odour concern is located adjacent to the concerned location. Nevertheless, the Contractor was reminded to review the handling procedures in case of any future marine sediment handling at the concerned location and to consider the implementation of mitigation measures as appropriate to minimize potential	
150904	01 Sept 2015	EPD Ref.: H05/RS/0002 2241-15 dated 04 September 2015 received by ET on 4 September 2015	East of New WanChai Ferry Pier	Dropping of excavated material from land to sea during laoding of material	 malodour impact to nearby public. A public complaint regarding dropping of excavated material from land to sea referred by EPD was received by ET on 04 September 2015 (EPD Ref.: H05/RS/00022241-15 dated 04 September 2015). The complainant reported that dropping of excavated materials from land to sea during loading of materials by excavator at the construction site to work boat. (Contract HK/2009/02) ET confirmed with the Resident Site Staff that transferring of C&D materials from land to hopper barge by excavator at seaside along CWB Tunnel Portions 3 and 4 was undertaken by Contract HK/2009/02 on 01 September 2015. Mitigation measure including providing tarpaulin sheet to cover the gap between seawall and the hopper barge to prevent dropping of material to the sea was implemented by the Contractor. According to the relevant site records under Contract HK/2009/02, transferring of C&D materials from land to hopper barge by excavator at seaside along CWB Tunnel Portions 3 and 4 was carried out on 01 September 2015 and mitigation measures including provision of tarpaulin sheet between 	Interim report submitted to EPD on 14 September 2015. EPD advised no comment on 5 October 2015 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					 seawall and the hopper barge was implemented by the Contractor of HK/2009/02 on the concerned date. Follow-up inspection was conducted during weekly environmental inspection on 10 September 2015. Transferring of C&D materials from land to barge by excavator was observed at the concerned location and mitigation measures including provision of tarpaulin sheet between seawall and hopper barge and the material transfer works was generally in order. Nevertheless, the Contractor of HK/2009/02 was reminded to maintain the handling procedure for C&D materials transfer from land to hopper barge and regularly inspect the condition of the tarpaulin sheet provided to ensure the nearby water quality are not affected by the loading and unloading of material from land side to hopper barge. The Contractor was reminded to maintain the handling procedure for C&D materials transfer from land to hopper barge and regularly inspect the condition of the tarpaulin sheet provided to ensure the nearby water quality are not affected by the loading and unloading of material from land side to hopper barge. 	
150904	02 Sept 2015	EPD Ref.: H04/RS/0002 2385-15 dated 04 September 2015 received by ET on 04 September 2015	Location outside Fleet Arcade	Construction noise was generated from the construction site of HK/2012/08 at location outside Fleet Arcade during night time on weekdays and daytime during General Holidays. The complainant also concerned construction dust and exhaust emission from derrick barges during	A public complaint regarding construction noise and dust and exhaust emission referred by EPD was received by ET on 04 September 2015 (EPD Ref.: H04/RS/00022385-15 dated 04 September 2015). The complainant reported that construction noise was generated from the construction site of HK/2012/08 at location outside Fleet Arcade during night time on weekdays and daytime during General Holidays. The complainant also concerned construction dust and exhaust emission from derrick barges during transporting C&D material at the site. (Contract HK/2012/08)	Interim report submitted to EPD on 14 September 2015. 2 nd interim report submitted to EPD on 17 Dec 2015



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				transporting C&D material at the site.	 ET confirmed with the Resident Site Staff that from 0800 hrs to 1800 hrs on 30 August 2015, removal of scaffold and timber and installation of bulkhead was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one generator and one circular saw were in operation. From 1900hrs on 30 August 2015 to 0700 on 31 August 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 1900hrs on 31 August 2015 to 0700 hrs on 01 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 1900hrs to 2115 hrs on 01 September 2015, unloading of soil was undertaken by the Contractor of HK/2012/08 at the concerned location. From 2300hrs on 01 September 2015 to 0700hrs on 02 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 2300hrs on 01 September 2015 to 0700hrs on 02 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 2300hrs on 01 September 2015 to 0700hrs on 02 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. From 2300hrs on 01 September 2015 to 0700hrs on 02 September 2015, no construction works was undertaken by the Contractor of HK/2012/08 at the concerned location. One derrick barge was deployed for unloading of soil on 02 September 2015 during daytime under Contract HK/2012/08 at the concerned location. One derrick barge was deployed for unloading of soil on 02 September 2015 during daytime under Contract HK/2012/08 at the concerned location. Based on the relevant site records, from 0800 hrs to 	3 rd interim report submitted to EPD on 31 Dec 2015
					1800 hrs on 30 August 2015, removal of scaffold	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					and timber and installation of bulkhead was	
					undertaken by the Contractor of HK/2012/08 at the	
					concerned location. Total one generator and one	
					circular saw were in operation and the relevant	
					Construction Noise Permit GW-RS0296-15 for the	
					concerned operation was confirmed in place.	
					From 1900hrs on 30 August 2015 to 0700 on 31	
					August 2015, no construction works was undertaken	
					by the Contractor of HK/2012/08 at the concerned	
					location and from 1900hrs on 31 August 2015 to	
					0700hrs on 01 September 2015, no construction	
					works was undertaken by the Contractor of	
					HK/2012/08 at the concerned location.	
					From 1900hrs to 2115 hrs on 01 September 2015,	
					unloading of soil was undertaken by the Contractor	
					of HK/2012/08 at the concerned location. Total one	
					derrick barge was in operation and the Construction	
					Noise Permit GW-RS0296-15 for the concerned	
					operation was confirmed in place.	
					From 2300hrs on 01 September 2015 to 0700hrs on	
					02 September 2015, no construction works was	
					undertaken by the Contractor of HK/2012/08 at the	
					concerned location. In view of the above, the	
					construction activities conducted under Contract	
					HK/2012/08 during the concerned period was in	
					compliance with the statutory requirement.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					In addition, one derrick barge was deployed for	
					unloading of soil on 02 September 2015 during	
					daytime under Contract HK/2012/08 at the	
					concerned location. Follow-up inspection was	
					conducted during weekly environmental inspection	
					on 08 September 2015 and no dark smoke emission	
					was observed from the derrick barge moored	
					outside the concerned location. Nevertheless, the	
					Contractor of HK/2012/08 was reminded to conduct	
					regular checking on the condition of the all derrick	
					barges deployed on site to ensure only well	
					maintained equipment are used to avoid potential	
					dark smoke emission affecting nearby public and	
					the Contractor of HK/2012/08 was reminded to	
					upkeep the site control system for construction	
					works carrying out at restricted hours and night time	
					for Construction Noise Permit compliance.	
					The Contractor was reminded to conduct regular	
					checking on the condition of derrick barges	
					deployed on site to ensure only well maintained	
					equipments are used on site to avoid potential dark	
					smoke emission affecting nearby public.	
L					The Contractor of HK/2012/08 was reminded to	
					upkeep the site control system for construction	
					works carrying out at restricted hours and night time	
					for Construction Noise Permit compliance.	



151117 Not specified EPD complaint received by ET on 17 Novmeber Causeway Bay Typhoon Shelter Improper handling or bentonite and marine sediment generated from construction works and construction to run November 2015. The complainant reported that over 10.000 m3 of bentonite after 2015 A public complaint regarding illegal disposal of construction of diaphragm wall was disposed of at Victoria Habour. Interim movember 2015. 151117 Not received by ET on 17 November 2015 Causeway Bay Typhoon Shelter Improper handling or construction or disphragm wall was disposed of at Victoria Habour. A public complainant report disphragm wall was disposed of at Victoria Habour. Improper handling or construction of disphragm wall was disposed of at Victoria Habour. Improper handling or construction of disphragm wall was disposed of at Victoria Habour. Improper handling or construction of disphragm wall was disposed of at Victoria Habour. Improper handling or construction at was the mixed with soil and transported to the Public Fill. During the course, waters and the soil mixing generated dust impact on earby yacht club, typhono shelter and diffect nearby public and boats. 2 rd interim investigation report submitted o Dredged/Exavated Sediment. Instead the marine sediment was covered by sand and soil and transported to the Public Fill. Final investigation report submitted on S February 2015. Final investigation report submitted on S February 2016. Final investigation report submitted on S February 2016. Final investigation report submitted on S February 2016.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					have been conducted by the ET and the	
					investigation findings were included in the interim	
					investigation reports separately submitted to the	
					EPD. In addition, the ET and IEC have conducted	
					checking on the waste disposal records and site	
					construction records with the CWB RSS team to	
					confirm the key construction activities during the	
					concerned period and the quantities of inert C&D	
					material disposed.	
					Specific enhancement on site supervision was	
					undertake by the CWB RSS team to ensure the	
					properly handling of the remaining bentonite slurry	
					in terms of the following:	
					Depth of the bentonite slurry at the primary mixing	
					pit (at south of TS3) was recorded by RSS team	
					daily at regular intervals starting from 22nd	
					December 2015 to record the changes in the level	
					of slurry, particularly before end of works and at the	
					start of works on the next day to confirm no	
					significant change in bentonite slurry level during	
					non-working hours until the complete removal of the	
					mud pit.	
					During the silo dismantling stage, the amount of	
					residue bentonite cleared from the remaining silo	
					were monitored on daily basis to record of the	
					residue bentonite transferred for mixing and final	
					disposal.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
-					The Environmental Team will continue to keep in	
					view on the contractor environmental mitigation	
					measures during the routine inspections, with	
					specific attention at TS3 area on the effectiveness	
					of Contractor's remediation measures and check the	
					implementation of site measures in accordance with	
					the EIA and EM&A Manual recommendations.	
ICC	26 No	ICC complaint	Construction area	Noise nuisance due to	A public complaint regarding noise impact referred	Final
complaint	2015	received by	outside City	windblown slapping of a	by RSS was received by ET on 27 November 2015	investigation report to be
case (ICC Ref: 2-		ET on 27 November	Garden Block 11	metal onto adjacent barrier at night time	(ICC Case Ref.: 2-1593165694 dated 26 November	issued on 01
159316569		2015		at hight time	2015). The complainant reported that noise was	December
4)					emanated from the IECL construction site outside	2015.
dated 26					City Garden Block 11 due to the windblown slapping	
November					of a metal sheet onto adjacent barrier causing	
2015					nuisance to nearby residents at night time.	
					ET confirmed with the Resident Site Staff that the	
					noise nuisance was caused by the windblown action	
					of the corrugated metal sheet loosely affixed onto	
					the temporary noise barrier panel above a concrete	
					block footing fronting City Garden.	
					The noise nuisance was caused by the windblown	
					action of the corrugated metal sheet loosely affixed	
					onto the temporary noise barrier panel above a	
					concrete blocking footing fronting City Garden. The	
					concerned corrugated metal sheet was removed by	
					the Contractor of HY/2009/19 on 27 November 2015	
					to avoid further generation of noise nuisance.	



Date of omplaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				The Contractor was reminded to check and ensure metal sheetings and other material stored within the construction site are properly affixed to avoid potential noise nuisance due to windblown action.	
 2 lovemb or 2015	EPD complaint received by ET on 04 December 2015	Two International Finance Centre at Finance Street, Central	Construction dust generated from construction site near Two International Finance Centre	A public complaint regarding construction dust impact referred by EPD was received by ET on 04 December 2015 (EPD Ref: H04/RS/00028924-15). The complainant reported that excessive construction dust was generated from the construction site near Two International Finance Centre at Finance Street, Central ET confirmed with the Resident Site Staff that bridge works and drains/ sewers construction at the concerned location was undertaken by Contract HY/2009/18 on 12 November 2015. A stockpile which would be reused for backfilling was stored at the concerned location by Contract HY/2009/18 on 12 November 2015. Mitigation measures implemented by the Contractor for the above construction works including covering of idled portion of stockpile and dampening of the exposed stockpile was implemented for the stockpile at the concerned location.	1 st interim report submitted to EPD on 14 December 2015 2 nd interm report suibmitted to EPD on 4 January 2016 EPD advised no comment on 07 January 2015 on the report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to relevant site records confirmed by	
					RSS, bridge works and drains/ sewers construction	
					at the concerned location was undertaken by	
					Contractor of HY/2009/18 on 12 November 2015	
					and a stockpile which would be reused for	
					backfilling was stored at the concerned location.	
					Mitigation measures including covering of idled	
					portion of stockpile and dampening of the exposed	
					stockpile was implemented for the stockpile at the	
					concerned location.	
					In view of the public concern on potential dust	
					impact at the concerned location, the Contractor of	
					HY/2009/18 rearranged the works sequence and	
					placed concrete blocks at the bridge retaining wall	
					to allow for early commencement of backfilling on	
					19 November 2015 to minimize the size of the	
					stockpile at an earlier stage. Additional water	
					sprinklers were installed on 27 November 2015 to	
					further enhance the dampening of the stockpile	
					surface during excavation.	
					Follow-up inspection was conducted during weekly	
					environmental inspection on 10 December 2015 and	
					mitigation measures including covering of stockpile	
					stored at the concerned location was implemented	
					while it was observed that stockpiles stored near	
					Man Chiu Street was not properly covered. The	
					Contractor of HY/2009/18 was advised to promptly	
					provide covering to all idled stockpile stored on site	
					and the Contractor was reminded to enhance the	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					watering during excavated material handling near	
					the concerned location. Further follow up inspection	
					was conducted on 17 December 2015 and	
					mitigation measures including covering and	
					watering for idle stockpile and material handling	
					were implemented.	
					A public complaint regarding noise impact referred	Final report
ICC complaint	14 Decemb	EPD complaint	Construction area outside City	Incessant noise emanating from the construction site	by RSS was received by ET on 16 December 2015	was issued on
case (ICC	er 2015	received by	Garden Block 10	of the Island East Corridor	(ICC Case Ref.: 2-1656689815 dated 14	23 December
Case Ref:		ET on 04	and Block 11	link that forms part of the	December 2015). The complainant reported that:	2015 and case closed.
2- 165668981		December 2015		Central Wanchai Bypass Project	becember 2013). The complainant reported that.	case closed.
5					Incessant noise emanating from the construction	
dated 14					site of the Island Eastern Corridor Link that forms	
December 2015					part of the Central-Wanchai Bypass Project.	
					Over the past couple of weeks, there have been	
					loud mechanical pounding at the construction site	
					over the reclaimed area between Blocks 10 and 11	
					of City Garden. As can be seen, machines have	
					been breaking open the concrete paved on top of	
					the reclaimed area. Work often starts well before	
					9am on weekdays and, barring a brief period of lull	
					during lunch hours, would often continue unabated	
					untill after 5pm. Although I note that certain noise	
					reduction measures have been put into place (e.g.	
					the erection of flimsy noise barriers around the work	
					area), the noise created is still enormous, and this	
					has become a significant nuisance for residents	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					living in nearby blocks of our estate, especially	
					children and the elderly who have to stay at home	
					for longer hours.	
					ET confirmed with the Resident Site Staff that	
					concreting breaking works was carried out with one	
					breaker on 7, 9, 11, 12 and 14 December 2015 and	
					the breaking works at the concerned location were	
					completed on 14 December 2015 morning. Noise	
					mitigation measures including temporary noise	
					barriers near the point of breaking and covering the	
					breaker with acoustic mat were provided during the	
					concerned concrete breaking works.	
					According to information confirmed by RSS,	
					concreting breaking works was carried out by one	
					excavator mounted breaker on 7, 9, 11, 12 and 14	
					December 2015 and the concerned breaking works	
					outside City Garden Block 10 and Block 11 was	
					completed on 14 December 2015 morning. Noise	
					mitigation measures including temporary noise	
					barriers near the point of breaking and covering the	
					breaker with acoustic mat were provided during the	
					concerned concrete breaking works. Based on the	
					further review on the record of the environmental	
					inspection conducted on 09 December 2015, the	
					Contractor of HY/2009/19 was reminded to	
					temporary noise barrier provided for the pile cap	
					demolition shall follow the the Environmental Permit	
					EP-364/2009/D requirement.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow up inspection was conducted during weekly	
					environmental inspection on 17 December 2015, the	
					concerned breaking works opposite to City Garden	
					Block 10 and Block 11 was observed completed	
					while the Contractor was reminded that the	
					remaining section of temporary noise barrier in	
					accordance with the latest Environmnetal Permit	
					EP-364/2009/D shall be completed on site as soon	
					as possible. According to the information provided	
					by RSS, the temporary noise barrier in accordance	
					with the Environmental Permit requirement opposite	
					to City Garden was substaintially completed on 21	
					December 2015. In view of the public concern, the	
					Contractor was suggested to consider to review the	
					works duration at daytime and conduct other future	
					breaking works around the concerned location	
					intermittently to minimize the potential noise	
					nuisance caused to the surroundings.	
EPD Ref.: H05/RS/00 000570-16 dated 14 January 2016	07 January 2016	EPD complaint received by ET on 14 January 2016	Lung King Street	Operation of powered mechanical equipment at the construction site near Lung King Street after 1900hrs.	A public complaint regarding construction noise referred by EPD was received by ET on 14 January 2016 (EPD Ref.: H05/RS/00000570-16 dated 14 January 2016). The complainant reported that there was operation of powered mechanical equipment at the construction site near Lung King Street after 1900hrs. (Contract HK/2012/08) ET confirmed with the Resident Site Staff that from 1900hrs to 2115hrs on 06 January 2016, shifting of equipment and socket H-pile casing was undertaken by the Contractor of HK/2012/08 at the concerned location. Total one crawler crane was in operation.	Interim investigation report submitted to EPD on 22 January 2016. EPD advised on 17 February no comment on the interm report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to the relevant site records provided by RSS, shifting of equipment and socket H-pile casing was undertaken by the Contractor of HK/2012/08 at the concerned location from 1900hrs to 2115hrs on 06 January 2016. Total one crawler crane was in operation and the relevant Construction Noise Permit GW-RS0976-15 for the concerned operation was confirmed in place. Based on the above, the construction activities conducted under Contract HK/2012/08 on 06 January 2016 after 1900hrs was in compliance with the statutory requirement. Nevertheless, the Contractor was reminded to upkeep the site control system for construction works carried out during restricted hours and night time for Construction Noise Permit compliance in view of the nearby	
ICC complaint case (ICC Ref.: #2- 1754682833 and ICC Ref: #2- 1759629742	19 January 2016	EPD complaint received by ET on 19 January 2016	Hung Hing Road	Drainage at Hung Hing Road, Causeway Bay near the entrance of Cross Harbour Tunnel was blocked and sewage was overflowing from the sewer.	public concern.Two public complaints regarding the subject matter on blocked drainage were referred by RSS was received by ET on 19 January 2016 (ICC Ref.: #2- 1754682833 and ICC Ref: #2-1759629742).The first complainant (ICC Ref.: #2-1754682833) on 11 January 2016 reported that the drainage at Hung Hing Road, Causeway Bay near the entrance of Cross Harbour Tunnel was blocked and sewage was overflowing from the sewer.The first complainant on 13 January 2016 enquired the status of follow-up, the complainant reported that the sewage overflow was severe and pose environmental hygiene concern to the	Final investigation report issued on 27 January 2016



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					surroundings.	
					The first complainant on 14 January 2016 reported that the situation was not improved and would escalate the case if not addressed.	
					The second complainant on 12 January 2016 (ICC Ref: #2-1759629742) reported that a foul sewer was found choking and foul water flows onto the carriageways.	
					ET confirmed with the Resident Site Staff that no discharge point from the Contractor of HY/2009/15 is located within the concern portion of public drain (roadside gully) along Hung Hing Road.	
					The observed yellow pipe extending from the roadside gully at Hung Hing Road into the site area under Contract HY/2009/15 was installed by the Contractor of HY/2009/15 to pump excessive sewage from the roadside gully on 11 January 2016.	
					According to relevant site records and information provided by RSS, a steady flow of wastewater, noticeably sewer-like odour, was seeping through an existing sewage manhole at Hung Hing Road on 11 January 2016 and resulting in the formation of local ponding formed around the low point gully nearby.	
					Based on relevant site information, no discharge point from the Contractor of HY/2009/15 was located at the concerned public drain (roadside gully) along Hung Hing Road while the observed yellow pipe extending from the roadside gully at Hung Hing Road into Contract HY/2009/15 site area was installed by the Contractor of HY/2009/15 to pump excessive sewage from the roadside gully and the logger 2016. In view of pa	
					roadside gully on 11 January 2016. In view of no discharge point established under Contractor HY/2009/15 was observed at the concerned portion of Hung Hing Road, no direct information	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					indicating the association with the Contractor of HY/2009/15 is considered available. Follow up inspection was conducted during the weekly environmental inspection on 26 January 2016, no further accumulation of wastewater and no particular blockage of the concerned roadside gully at Hung Hing Road was observed. In addition, no overflow from the roadside sewer was observed. Nevertheless, the Contractor of HY/2009/15 was reminded to upkeep the site exit condition to avoid any potential impact to the surroundings.	
EPD complaint case (EPD Case Ref.:H05/R S/00001524 -16	22 January 2016	EPD complaint received by ET on 22 January 2016	Hung Hing Road	Construction wastewater from the China Stat's construction site under Contract HY/2009/15 was discharged from the site exit at Hung Hing Road near the Royal Hong Kong Yacht Club to the carriage of Hung Hing Road causing accumulation of stagnant water	A public complaint regarding the blockage of public drainage referred by EPD was received by ET on 22 January 2016 (EPD Case Ref.: H05/RS/00001524-16). The complainant reported that construction wastewater from the China State's construction site under Contract HY/2009/15 was discharged from the site exit at Hung Hing Road near the Royal Hong Kong Yacht Club to the carriage of Hung Hing Road causing accumulation of stagnant water starting from 11 January 2016. ET confirmed with the Resident Site Staff that no construction activities with potential runoff at the main entrance of PRE Office was conducted under Contractor of HY/2009/15 on 11, 14, 15 and 17 January 2016. Concreting for Seawall Reinstatement at TPCWAE was conducted under Contractor of HY/2009/15 on 12 January 2016 and 18 January 2016. Concreting for construction works at covered Tunnel by using concrete pump at TPCWAE was conducted under Contractor of HY/2009/15 on 13 January 2016 and 16 January 2016.	Interim investigation report submitted to EPD on 01 February 2016. EPD advised on 17 February no comment on the interm report submitted and case closed.
					According to relevant site records and information	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Nature of Complaint	provided by RSS, a steady flow of wastewater, noticeably sewer-like odour, was seeping through an existing sewage manhole at Hung Hing Road on 11 January 2016 and resulting in the formation of local ponding formed around the low point gully nearby. Based on relevant site information provided by RSS, no construction activity with potential runoff at the main entrance of PRE Office were conducted under Contractor of HY/2009/15 on 11, 14, 15 and 17 January 2016 while concreting for seawall reinstatement at TPCWAE were conducted on 12 January 2016 and 18 January 2016 and concreting for construction works at covered Tunnel by using concrete pump at TPCWAE were conducted on 13 January 2016 and 16 January 2016. All construction runoff was pumped to the wastewater treatment facility. In	Status
					addition, no discharge point from the Contractor of HY/2009/15 was located at the concerned public drain (roadside gully) along Hung Hing Road. Follow up inspection was conducted during the weekly environmental inspection on 26 January 2016. No further accumulation of wastewater and particular blockage of the concerned roadside gully at Hung Hing Road was observed and no overflow from the roadside sewer was observed. The condition of the construction site exit under HY/2009/15 was generally in order and no particular construction surface runoff was observed. Nevertheless, the Contractor of HY/2009/15 was reminded to upkeep the site exit condition to avoid any potential impact to the surroundings.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref.: H05/RS/000 03169-16 dated 16 February 2016	16 February 2016	EPD complaint received by ET on 16 February 2016	West of HKCEC	Construction work at construction site of CEDD Wan Chai Development Phase II reclamation project around 2200hrs	A public complaint regarding construction works at restricted hours referred by EPD was received by ET on 16 February 2016 (EPD Ref.:H05/RS/00003169-16 dated 16 February 2016). The complainant reported that: There was construction work at construction site of CEDD Wan Chai Development Phase II reclamation project around 2200hrs on 06 February 2016 at the west of HKCEC within the work area of Contract HK/2012/08. ET confirmed with the Resident Site Staff that from 1900hrs to 2300hrs on 06 February 2016, no site activity was undertaken by the Contractor of HK/2012/08 at the concerned location and site activities under the Contractor of HK/2012/08 at the concerned area were stopped around 1700hrs on 06 February 2016. According to the relevant site records provided by RSS, from 1900hrs to 2300hrs on 06 February 2016, no site activity was undertaken by the Contractor of HK/2012/08 at the concerned location and site activities under the Contractor of HK/2012/08 at the concerned area were stopped around 1700hrs on 06 February 2016. Nevertheless, the Contractor was reminded to upkeep the site control system for any construction works carried out during restricted hours and night time for Construction Noise Permit compliance.	Interim investigation report submitted to EPD on 23 February 2016.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC Ref.: CASE#2- 193863740 3 dated 01 March 2016	CASE#2- 2016 received b 193863740 on 03 Ma 3 dated 01 2016	ICC complaint received by ET on 03 March 2016	Lung King Street near the parking spaces for motorcycles	Construction noise was emanated from road works	A public complaint regarding construction noise referred by ICC was received by ET on 03 March 2016 (ICC Ref.: CASE#2-1938637403 dated 01 March 2016). The complainant reported that construction noise was emanated from road works located between Lung Wo Road and Lung Wui Road Interface. Further information was referred by RSS on 15 March 2016, the complainant clarified on 15 March 2016 that construction noise was emanated from road works located between Lung Wo Road and Lung Wui Road Interface during midnight and has lasted for one and half month resulting in nuisance to nearby residence.	1 st investigation report issued on 11 March 2016. 2 nd investigation report issued on 23 March 2016 and case closed.
					Further information was referred by RSS on 18 March 2016, the complainant further clarified on 18 March 2016 that the concerned location shall be Lung King Street near the parking spaces for motorcycles and the Contract no. as stated on the publicity board is HK/2012/08. Furthermore, the complainant identified the noise was from power generators.	
					ET confirmed with the Resident Site Staff that there was neither construction works nor operation of power generators under Contract HK/2012/08 at the concerned location from 1900hrs to 0700hrs during the period from 23 February 2016 to 14 March 2016.	
					Based on the complaint information referred by ICC on 3 March 2016, according to the relevant site records provided by RSS, from 0800hrs to 1800hrs on both 29 February 2016 and 01 March 2016, drainage works was undertaken by Contract HK/2012/08 at Lung Wo Road and one excavator was in operation for soil excavation. Follow up inspection was conducted during the weekly environmental site inspection on 08 March 2016	





Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref.: H05/RS/000 05206-16 dated 10 March 2016	07 March 2016	EPD complaint received by ET on 10 March 2016	Waterfront at Lung King Street	Construction dust, plant exhaust and construction noise generated from the construction work of Contract HK/2012/08 at waterfront of Lung King Street caused nuisance, and the water quality at the waterfront of Lung King Street was becoming worse that accumulation of the floating refuse and foam was found	A public complaint regarding construction dust, plant exhaust, construction noise and water quality referred by EPD was received by ET on 10 March 2016 (EPD Ref.: H05/RS/00005206-16 dated 10 March 2016). The complainant reported that construction dust, plant exhaust and construction noise generated from the construction work of Contract HK/2012/08 at waterfront of Lung King Street caused nuisance, and the water quality at the waterfront of Lung King Street was becoming worse that accumulation of the floating refuse and foam was found. ET confirmed with the Resident Site Staff that soil excavation at ELS area, Zone A2(2), was carried out, where at approx. 100m from the waterfront of Lung King Street from 08:00 hrs to 18:00 hrs on 07 March 2016 under Contract HK/2012/08. Two excavators were involved at that location. Erection of falsework for culvert L was carried out near the waterfront of Lung King Street from 08:00 hrs to 18:00 hrs on 07 March 2016 under Contract HK/2012/08. One lorry crane was involved for lifting falsework elements. Dust suppression measures including the water sprinklers were installed along site haul road. Regularly removed the floating refuse at the waterfront of Lung King Street was conducted by the Contractor of HK/2012/08. The concerned observed floating foam at the waterfront of Lung King Street was found originating from the diverted cooling mains discharge. According to the relevant site records provided by RSS, soil excavation at ELS area, Zone A2(2) was carried out, where at approx.100m from the waterfront of Lung King Street under Contract	Interim investigation report submitted to EPD on 18 March 2016. EPD advised no comment on 29 April 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					 HK/2012/08 from 08:00hrs to 18:00hrs on 07 March 2016 and two excavators were in operation at that location while erection of falsework for culvert L was carried out near the waterfront of Lung King Street from 08:00hrs and 18:00hrs on 07 March 2016 under Contract HK/2012/08 and one lorry crane was involved for lifting falsework elements. Dust suppression measures including the use of water sprinklers along the site haul road was implemented by the Contractor of HK/2012/08 and removal of floating refuse was regularly conducted at the waterfront of Lung King Street by the Contractor of HK/2012/08. Upon investigation, the concerned observed floating foam at the waterfront of Lung King Street cooling mains discharge. Follow up inspection was conducted during the weekly environmental site inspection on 15 March 2016 and dust suppression measures including watering for haul road, tarpaulin sheet covering for cement bags stored on site and three side and top covering for grouting station were implemented while and no dark smoke emission from the plant and machinery deployed on site was observed. Noise mitigation measures including refuse on site was observed implemented by the Contractor of HK/2012/08 and no accumulation of floating refuse was found. The concerned foam originating from diverted cooling mains discharge was observed implemented by the Contractor of HK/2012/08 and no accumulation of floating refuse on site was observed implemented by the Contractor of HK/2012/08 and no accumulation of floating refuse was found. The concerned foam originating from diverted cooling mains discharge was observed isolated from the nearby public area. 	
					Nevertheless, in view of the public concern, the	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Contractor was recommended to maintain regular checking of the plants and equipment deployed on site to avoid potential air quality impact to the nearby public and to maintain adequate dust suppression measures on site to avoid potential dust impact to the surroundings. The Contractor was reminded to maintain regular cleaning of floating refuse within the construction site area to avoid potential nuisance to the surroundings. The Contractor was also reminded to maintain the noise mitigation measure if breaking works would be required. The Contractor was also suggested to reflect the observed foam to relevant Cooling Mains owners.	
EPD Ref.: H05/RS/000 06732-16 dated 10 March 2016	23 March 2016	EPD complaint received by ET on 31 March 2016	Seafront opposite to City Garden	Muddy water discharge from construction site outside City Garden	A public complaint regarding direct discharge of muddy effluent referred by EPD was received by ET on 31 March 2016 (Case Ref.: H08/RS/00006732-16). The complainant reported that:	The interim investigation report was submitted to EPD on 11 April 2016.
					Muddy water was observed discharged from the construction site of Central – Wan Chai Bypass – Tunnel (North Point Section) and Island Eastern Corridor Link (Contract No. HY/2009/19) into Victoria Habour via a drain hole.	EPD advised no comment on 02 September 2016 on the
					ET confirmed with the Resident Site Staff that pipe Laying works between Pier 32 and Pier 33 and excavation and blinding works for Manhole at Pier 34 were in progress on 22 March 2016.	interim report submitted and case closed.
					The observed drain hole was identified to be the outlet point of a manhole and a section of an abandoned U-channel (extending from the concerned manhole to the Hong Kong Electric Substation in length along the site boundary) was adjoining the concerned manhole and sandbag was previously placed at the U-channel at the location near the inlet point to the concerned manhole.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Based on the site records confirmed by RSS, pipe laying works between Pier 32 and Pier 33 and excavation and blinding works for Manhole at Pier 34 were in progress on 22 March 2016. The observed drain hole was identified to be the outlet point of a manhole and a section of an abandoned U-channel (extending from the concerned manhole to the Hong Kong Electric Substation in length along the site boundary) was adjoining the concerned manhole and sandbag was previously placed at the U-channel at the location near the inlet point to the concerned manhole. In addition, no site discharge point was connected to the aforesaid U-channel and the concerned manhole. In view of the environmental concern, the following remedial and precautionary actions were taken by	
					 the Contractor of HY/2009/19 on 29 March 2016. i)Plugging the inlet point of the concerned manhole (connecting to the abandoned U-channel) with concrete; ii)Plugging the outlet of the concerned manhole (connecting to the observed drain hole) with concrete; iii)Filling the concerned manhole with rubbles; iv)Shifting the unused wastewater treatment plant around the concerned location to other site location for use. 	
					Follow-up inspection was conducted by the Environmental Team on 06 April 2016. No further contaminated runoff discharge was observed from the concerned drain hole and precautionary measures including provision of concrete bunding was implemented along the site boundary at the concerned location to avoid potential surface overflow. The pipe laying works and the excavation works was found at distant location	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					away from the concerned drain hole with no surface drain connection and no particular effluent was generated from the work. As such, no information indicate the discharge was related to the above construction activities.	
					However, it was noted that another section of surface drainage channel within the construction site (perpendicular in direction to the initial identified abandoned U-channel) was also in connection to concerned manhole and minor residue mud deposition was observed within the surface drainage channel. Despite the above additional surface drainage channel identified, the outlet point of concerned final manhole (in connection with the observed drain hole) was observed plugged with concrete and filled with rubbles as rectification measure to avoid any further contaminated runoff discharge via the observed drain hole.	
					Nevertheless, the Contractor of HY/2009/19 was reminded to conduct regular cleaning works for site surface drainage channel to avoid accumulation of silt and soil and avoid potential overflow by directing the surface runoff within the surface drainage channel to proper collection point for necessary treatment prior to discharge. The Contractor of HY/2009/19 was also reminded to check and review other surface drainage channel within the construction site to avoid potential runoff related impact via surface drainage channel to the nearby waters.	
					In addition, it was noticed that water was discharged from a piping extending from City Garden and the discharged water would result in seepage across the site hoarding into the abandoned U-channel. The Contractor of HY/2009/19 was suggested to liaise with the City Garden Management Office for proper connection	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					of the observed pipping with discharge to prevent further seepage water into the construction site.	
H08/RS/000 07662-16	05 April 2016	EPD complaint received by ET on 05 April 2016	Construction area opposite to Harbour Heights	Construction dust emission arising from drilling activity	A public complaint regarding construction dust emission was referred by EPD was received by ET on 05 April 2016 (Case Ref.: H08/RS/00007662- 16). The complainant reported that construction dust emission arising from drilling activity from the construction site of Central – Wan Chai Bypass – Tunnel (North Point Section) and Island Eastern Corridor Link (Contract No. HY/2009/19). ET confirmed with the Resident Site Staff that drilling holes for installation of starter bars was carried out under Contract HY/2009/19 at the vertical cut face of the existing IEC road slab on 05 April 2016 Based on the site records confirmed by RSS, drilling holes for installation of starter bars was carried out under Contract HY/2009/19 at the vertical cut face of the existing IEC road slab on 05 April 2016 Based on the site records the photo information provided by the EPD, no dust suppression measures was implemented during the observed drilling works on 05 April 2016. According to Air Pollution Control Ordinance, for pneumatic or power-driven drilling, cutting and polishing, water or a dust suppression chemical shall be continuously sprayed on the surface where any pneumatic or power-driven drilling,	The interim report was submitted to the EPD on 14 April 2016. EPD conducted follow up site visit on rectification measures on 21 April 2016. A inspection record form (Pink Form) was issued to the Contractor regarding the observed incident. EPD advised no comment on 02 September 2016 on the interim report submitted and case closed.
					cutting, polishing or other mechanical breaking operation that causes dust emission is carried out, unless the process is accompanied by the operation of an effective dust extraction and filtering device.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow-up inspection was conducted on 06 April 2016, rectification actions including the use of vacuum suction to extract dust generated during the concerned drilling works was observed implemented by the Contractor of HY/2009/19 for starter bars drilling works.	
ICC Case Ref.:2- 203652505 5 dated 27 March 2016	27 March 2016	ICC complaint case received by ET on 11 April 2016	Victoria Park Road Pedestrian Pathway	Toppling of tree	 An ICC public complaint regarding landscape aspect was referred by RSS was received by ET on 11 April 2016 (Case Ref.:2-2036525055). The complainant reported that a tree (6 meters in height and 1.5 meters in diameter) was found toppled at 111 Victoria Park Road, near Lamp post 38632 and blocking the Pedestrian pathway on 27 March 2016. ET confirmed with the Resident Site Staff that the concerned tree was identified as T710 and no construction activity in the vicinity of tree T710 on 27 March 2016 and no construction works are required in or near its vicinity. Based on the site records confirmed by RSS, the concerned tree was identified as the retained tree T710 maintained under the Contract of HY/2010/08 and the concerned tree T710 was located outside the assessment area in the relevant Project EIA Report. No construction works are required in the vicinity of concerned tree T710 and no construction activity was conducted in the vicinity of tree T710 and no construction activity as conducted in the vicinity of tree T710 and no construction activity as conducted in the vicinity of tree T710 on 27 March 2016. Nevertheless, based on RSS information, recent tree monitoring report indicates an existing cavity at trunk and the concerned tree T710 has been recommended to be felled in the tree risk assessment Form 2. 	Investigation Report issued on 15 April 2016 and case closed
					With respect to the observed incident of the toppling of the concerned tree T710, the	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Contractor of HY/2010/08 was instructed by RSS to remove the broken trunk/ remains to avoid impact to the surroundings. The concerned tree T710 shall be compensated by the Contractor of HY/2010/08 in accordance with the Development Bureau Technical Circular (Works) No. 7/2015 and the detail on compensation would be further agreed with Victoria Park Management Office. Follow-up inspection was conducted on 13 April 2016, and the remaining parts of the concerned tree T710 was observed felled to avoid further impact to nearby public road.	
Not available	12 April 2016	A CEDD public complaint referred by RSS was received by ET on 13 April 2016	East of Star Ferry Piers	Muddy water was observed to disperse from Contract HK/2009/02 site area to Victoria Harbour occasionally as there was no silt curtain installed under the buoyancy floats. The location concerned was the East of Star Ferry Piers (Contract No. HK/2009/02).	 A CEDD public complaint regarding muddy dispersion referred by RSS was received by ET on 13 April 2016. The complainant reported that muddy water was observed to disperse from Contract HK/2009/02 site area to Victoria Harbour occasionally as there was no silt curtain installed under the buoyancy floats. The location concerned was the East of Star Ferry Piers (Contract No. HK/2009/02). ET confirmed with the Resident Site Staff that no marine construction activities or land construction activities under Contract HK/2009/02 at the concerned location on 12 April 2016. Surface runoff control measures including provision of concrete bund at the concerned location was implemented by Contract HK/2009/02. No soil & silt deposition along the seawall at the concerned location under Contract HK/2009/02. Silt curtain with buoyancy floats acting as anchor points was installed at Monitoring Station RW21-P789 for Water intakes. 	Investigation report issued on 19 April 2016 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					 Based on the site records confirmed by RSS, no marine construction activities or land construction activities was carried out under Contract HK/2009/02 at the concerned location on 12 April 2016 and no soil and silt deposition was found along the seawall at the concerned location and precautionary measures for site runoff control including provision of concrete bund along boundary of site area near the waterfront around the concerned location was implemented by the Contractor HK/2009/02. In addition, no discharge point under Contract HK/2009/02 was located in the vicinity of the concerned location. Based on information confirmed by RSS, the buoyancy floats deployed at the concerned location are acting as the anchor points for the silt curtain deployed around the WQM Station RW21-P789 for the WSD and Cooling Water Intakes group. Follow-up inspection was conducted on 14 April 2016, no surface runoff from the construction site nor discharge of contaminated effluent was observed around the concerned location and precautionary measures including the provision of concrete bund at the concerned location was observed maintained by the Contractor of HK/2009/02 and the silt curtain deployed around the WQM station RW21-P789 was generally in order. In view of the public concern on the water quality, the Contractor of HK/2009/02 was reminded to maintain effective surface runoff protection and provide proper collection point of construction effluent around the concerned location to avoid potential surface runoff related impact. 	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref.: H05/RS/000 08367-16 dated 13 April 2016	13 April 2016	A public complaint referred by EPD was received by ET on 13 April 2016	Outside the Hong Kong Academy for Performing Arts	Muddy water discharge from construction site	A public complaint regarding muddy water discharge referred by EPD was received by ET on 13 April 2016 (EPD Ref.: H05/RS/00008367-16 dated 13 April 2016). The complainant reported that muddy water was discharged from the construction work of Contract HK/2012/08 to the sea outside the Hong Kong Academy for Performing Arts on 13 April 2016 morning. ET confirmed with the Resident Site Staff that internal transport of soil to the hopper barge for storage via landing barge was conducted by Contractor of HK/2012/08 during 0800 hours to 1000 hours on 13 April 2016 at the sea outside the concerned location and 3 nos. of dump trucks were deployed for the operation. Protection measure including provision of sandbag bunding along the side of the landing barge was implemented by the Contractor of HK/2012/08. According to the relevant site records provided by RSS, internal transport of soil to the hopper barge for storage via landing barge was conducted by Contractor of HK/2012/08 during 0800 hours to 1000 hours on 13 April 2016 at the sea outside the concerned location and 3 nos. of dump trucks were deployed for the operation. Protection measure including provision of sandbag bunding along the side of the landing barge was conducted by Contractor of HK/2012/08 during 0800 hours to 1000 hours on 13 April 2016 at the sea outside the concerned location and 3 nos. of dump trucks were deployed for the operation. Protection measure including provision of sandbag bunding along the side of the landing barge was implemented by the Contractor of HK/2012/08. In addition, amber rainstorm warning signal was hoisted from 0630 hours to 1200 hours on 13 April 2016 and during the above time period, muddy water was observed from the upstream of culvert L outside the HK/2012/08 site.	Interim investigation report was submitted to the EPD on 21 April 2016. EPD advised no further comment on 06 June 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					sandbag bunding along the side of the landing barge was implemented and no mud or soil deposition was observed along the seawall and no discharge point was located within the temporary water channel connecting the Culvert L outfall location to the Victoria Harbour. In addition, piling works was observed at the north side of Zone A1 on 19 April 2016 and construction effluent collection from piling work via sedimentation tank to wastewater treatment facility was implemented and steel barrier was installed around the piling works area to mitigate against potential surface runoff related impact. Nevertheless, in view of the public concern, the Contractor was reminded to maintain adequate perimeter embankment protection along the seawall boundary and maintain proper construction effluent collection system to avoid potential runoff related impact to nearby waters.	
EPD Ref: H05/RS/000 12646-16 dated 27 May 2016	26 May 2016	A public complaint referred by EPD was received by ET on 27 May 2016	Construction Site near Wanchai Ferry Pier	Operation of generator around the clock	A EPD complaint regarding noise nuisance referred by RSS was received by ET on 27 May 2016 (EPD Ref: H05/RS/00012646-16 dated 27 May 2016). The complainant reported that a generator was operated round-the-clock in the Chun Wo- CRGL JV construction site near Wanchai Ferry Pier that cause noise nuisance. (Contract No. HK/2009/02). ET confirmed with the Resident Site Staff that a generator deployed under Contract HK/2009/02 near the covered walkway for Wanchai Ferry Pier at Portion 2 area and was operated from 1900hrs on 24 May 2016 to 0700hrs on 25 May 2016 and from 1900hrs on 25 May 2016 to 0700hrs on 26 May 2016. The generator was used for the power supply of lighting inside Tunnel Portions 1 and 2. According to the relevant site records provided by	Interim investigation report submitted to EPD on 7 June 2016. EPD advised no further comment on 05 August 2016 on the report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					RSS, a generator deployed under Contract HK/2009/02 near the covered walkway for Wanchai Ferry Pier at Portion 2 area and was operated from 1900hrs on 24 May 2016 to 0700hrs on 25 May 2016 and from 1900hrs on 25 May 2016 to 0700hrs on 26 May 2016. The generator was used for the power supply of lighting inside Tunnel Portions 1 and 2. Based on review on site information, relevant Construction Noise Permits GW-RS0516-16 and GW-RS0390- 16 for the operation of the concerned generator were confirmed in place while no sufficient site information was considered available to demonstrate the use of acoustic enclosure for the operation of the generator following the special condition 3d item 4. Despite the above, the Contractor of HK/2009/02 has suspended the use of the generator at the concerned location after 2300hours to minimize potential noise concern to the surroundings from 28 May 2016. Nevertheless, the Contractor of HK/2009/02 was reminded to upkeep the site control system for construction works carried out during restricted hours and night time for Construction Noise Permit compliance and maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref: H08/RS/000 14627-16 dated 16 June 2016	15 June 2016	A public complaint referred by EPD was received by ET on 16 June 2016	Construction area of Island Eastern Corridor near Sea View Estate.	Splashing from the working area of Island Eastern Corridor near Sea View Estate.	A public complaint was referred by EPD was received by ET on 16 June 2016 (Case Ref.: H08/RS/00014627-16). The complainant reported that his or her properties were covered by many water stains which were splashing from the working area of Island Eastern Corridor near Sea View Estate. ET confirmed with the Resident Site Staff that rebar fixing was carried out on 13 and 14 June 2016 under the Contractor of HY/2009/19 while formwork cleaning and laying concrete for stitching and curing work for concrete were carried out under the Contractor of HY/2009/19 on 15 June 2016 and 16 June 2016 respectively.	The interim report submitted to the EPD on 29 June 2016. EPD advised no comment on the interim report submitted and case closed on 02 September 2016.
					Mitigation measures including provision of metal cover underneath the bridge deck in slanting position at Watson Road to prevent spilling of water onto public road and provision of tarpaulin sheet along the guard rails of the bridge deck at Pier 19- 20 (opposite to Sea View Estate) to prevent splashing of water to outside area were implemented by the Contractor of HY/2009/19.	
					Based on the site records confirmed by RSS, rebar fixing was carried out on 13 and 14 June 2016 under the Contractor of HY/2009/19 while formwork cleaning and laying concrete for stitching and curing work for concrete were carried out under the Contractor of HY/2009/19 on 15 June 2016 and 16 June 2016 respectively.	
					Mitigation measures including provision of metal cover underneath the bridge deck in slanting position at Watson Road to prevent spilling of water onto public road and provision of tarpaulin sheet along the guard rails of the bridge deck at Pier 19- 20 (opposite to Sea View Estate) to prevent splashing of water to outside area were implemented by the Contractor of HY/2009/19.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Follow up inspection was conducted on 22 June 2016, mitigation measures including the use of metal cover underneath the bridge deck at Watson Road and provision of tarpaulin sheet along the guard rails of the section of bridge deck opposite to Sea View Estate were implemented by the Contractor of HY/2009/19. No particular spilling or splashing of construction water was observed during inspection around the concerned location. Nevertheless, in view of the public concern, the Contractor of HY/2009/19 was suggested that the direction of the water hose shall be pointed away from the public area as far as practicable during water use or watering for dust suppression to avoid potential splashing nuisance caused to the surroundings. The Contractor of HY/2009/19 was also reminded to maintain proper site drainage to direct surface runoff generated from construction works or cleaning to the proper collection point within site area to avoid potential nuisance to the surroundings.	
EPD Ref: H08/RS/000 16213-16 dated 14 July 2016	30 June 2016	A public complaint referred by EPD was received by ET on 14 July 2016	Construction Site of TS3 near Slip Road 8	Night time construction noise from construction works between 0200hrs to 0300hrs and construction dust emission from construction site of TS3 near Slip Road 8 section.	A public complaint referred by EPD was received by ET on 14 July 2016 (Case Ref.: H08/RS/00016213-16). The complainant reported the concern about night time construction noise from construction works between 0200hrs to 0300hrs and construction dust emission from construction site of TS3 near Slip Road 8 section. ET confirmed with the Resident Site Staff that excavation at TS3 and loading of material onto derrick barge (Shun Tat 28) by crawler crane was undertaken by the Contractor of HY/2010/08 from 19:00hrs to around 02:00hrs on 30 June 2016. Total one crawler crane was in operation. Noise mitigation measures including equipping the crawler crane with noise barrier was implemented	The interim report submitted to the EPD on 22 July 2016



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					by the Contractor of HY/2010/08.	
					Dust mitigation measures including manual spraying of water and mist nozzles are deployed on the ground level and at the cofferdam.	
					Based on the site records confirmed by RSS, excavation at TS3 and loading of material onto derrick barge (Shun Tat 28) by crawler crane was undertaken by the Contractor of HY/2010/08 from 19:00hrs on 29 June 2016 to around 02:00hrs on 30 June 2016. No construction works was conducted at the concerned location after around 02:00hrs on 30 June 2016. Total one crawler crane was in operation and noise mitigation measures including equipping the crawler crane with noise barrier was implemented by the Contractor of HY/2010/08.	
					Based on review on relevant record, Construction Noise Permit GW-RS0434-16 for the operation of crawler crane at the concerned location was in place. However, based on relevant site record, it was noted that the crawler crane deployed during the concerned period could not match with the specific PME requirement under condition 3a (Crane, crawler, mounted with noise barrier (Kobelco 7250S)) of the Construction Noise Permit GW-RS0434-16 between 23:00hrs to 07:00hrs on the following day. Dust mitigation measures including manual spraying of water and mist nozzles were deployed on the ground level and at the cofferdam.	
					Follow up inspection was conducted on 20 July 2016, the potential concerned excavation works at the concerned location was not observed and no particular dust impact was observed around the concerned location.	
					In view of the above, the Contractor of HY/2010/08 was advised to review the site control system for	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					construction works carried out during restricted hours to check and ensure the model/ specific PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public. Also, the Contractor of HY/2010/08 was reminded to maintain sufficient watering for excavated material handling to avoid potential dust nuisance to the surroundings.	
EPD Ref: H08/RS/000 22448-16 dated 06 September 2016	04 Sept 2016	A public complaint referred by EPD was received by ET on 06 September 2016	Road construction works area near Causeway Bay Typhoon Shelter	Construction noise from road construction work near Causeway Bay Typhoon Shelter	A public complaint referred by EPD was received by ET on 06 September 2016 (Case Ref.: H08/RS/00022448-16). The complainant reported that construction noise from the road construction work near Causeway Bay Typhoon Shelter during 0800hrs to 2100 hrs on 04 September 2016 (Sunday) caused nuisance. The complainant also indicated that the construction noise was generated up to 0100 hrs on normal weekdays. ET confirmed with the Resident Site Staff that underwater welding of lagging plate at Zone C was conducted from 0800hrs to 2100hrs on 04 September 2016. Total 1 no. of generator and 1 no. of welding machine were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 01 September 2016 to 0100hrs on 02 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 01 September 2016 to 0100hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 02 September 2016 to 0100hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 02 September 2016 to 0100hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation.	The interim report submitted to EPD on 20 September 2016. EPD advised no comment on 31 October 2016 on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					slow lane was conducted from 2300hrs to 2359hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation.	
					Based on the site records confirmed by RSS, underwater welding of lagging plate at Zone C was conducted from 0800hrs to 2100hrs on 04 September 2016, total 1 no. of generator and 1 no. of welding machine were in operation and relevant Construction Noise Permit GW-RS0442-16 was in place. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 01 September 2016 to 0100hrs on 02 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs on 02 September 2016 to 0100hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Grouting works at Victoria Park Road Eastbound slow lane was conducted from 2300hrs to 2359hrs on 03 September 2016. Total 1 no. of grout mixer, 1 no. of agitator and 1 no. of grout pump were in operation. Relevant Construction Noise Permit GW-RS0531-16 was in place for the above construction activities.	
					Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD Ref: H08/RS/000 24768-16 dated 07 October 2016	28 Sept 2016 04 Oct 2016	A public complaint referred by EPD was received by ET on 07 October 2016	Causeway Bay Typhoon Shelter	Construction work at the construction site in Causeway Bay Typhoon Shelter area was found after 1900hrs on 28 September 2016 and 04 October 2016 that caused noise nuisance.	 A public complaint referred by EPD was received by ET on 07 October 2016 (Case Ref.: H08/RS/00024768-16). The complainant reported that construction work at the construction site in Causeway Bay Typhoon Shelter area was found after 1900hrs on 28 September 2016 and 04 October 2016 that caused noise nuisance. The complainant also reported that there were 5 concrete lorry mixers operating at the above site after 1900hrs on 04 October 2016. ET confirmed with the Resident Site Staff that concreting for tunnel structure in TS3 (W) was conducted from 1900hrs to 2300hrs on 28 September 2016. One concrete pump and two concrete lorry mixers were in operation. One no. of concrete lorry mixer was located at the East of TS3 (W) and one no. of concrete lorry mixer was located from 1900hrs to 2300hrs on 200 Concrete pump and two concrete pump and two concrete lorry mixer was located at the East of TS3 (W) and one no. of concrete lorry mixer was located at the East of TS3 (W) and one no. of concrete lorry mixer was located at the East of TS3 (W) and one no. of concrete lorry mixer was located at the East of TS3 (W). Based on the site records confirmed by RSS, concreting for tunnel structure in TS3 (W) and one no. of concrete lorry mixer was located at the west of TS3 (W). Based on the site records confirmed by RSS, concreting for tunnel structure in TS3 (W) was conducted from 1900hrs to 2300hrs on 28 September 2016 and from 1900hrs to 2300hrs on 28 September 2016 and from 1900hrs to 2300hrs on 04 October 2016 and total one concrete pump and two concrete lorry mixers were in operation during the above concerned periods. One no. of concrete pump and two concrete pump an	The interim investigation report was submitted to EPD on 18 October 2016.
					tunnel structure in TS3 (W) was conducted from 1900hrs to 2300hrs on 04 October 2016. One concrete pump and two concrete lorry mixers were in operation. One no. of concrete lorry mixer was located at the East of TS3 (W) and one no. of concrete lorry mixer was located at the west of TS3 (W). Based on the site records confirmed by RSS, concreting for tunnel structure in TS3 (W) was conducted from 1900hrs to 2300hrs on 28 September 2016 and from 1900hrs to 2300hrs on 04 October 2016 and total one concrete pump and two concrete lorry mixers were in operation during the above concerned periods. One no. of concrete lorry mixer was located at the East of TS3 (W) and	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					GW-RS0434-16 and GW-RS0407-16 were in place for the construction works conducted during the above concerned periods.	
					Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
EPD Ref: H05/RS/0002 9722-16 dated 22 November 2016	15 Nov 2016	A public complaint referred by EPD received by ET on 22 November 2016	Construction Site near Wanchai Ferry Pier	Noise was emanated in the Chun Wo – CRGLJV construction site near Wanchai Ferry Pier till late night and caused nuisance to nearby sensitive receivers.	An EPD complaint regarding noise nuisance referred by EPD was received by ET on 22 November 2016 (EPD Ref: H05/RS/00029722-16 dated 22 November 2016). The complainant reported that noise was emanated in the Chun Wo – CRGLJV construction site near Wanchai Ferry Pier till late night and caused nuisance to nearby sensitive receivers.	Interim investigation report submitted to EPD on 29 November 2016.
					ET confirmed with the Resident Site Staff that Excavation works at Portion 5 was conducted under Contract HK/2009/02 at Portion 5 area (West of Wan Chai Ferry Pier) from 1900hrs to 2300hrs on 14 November 2016. Total two crawler cranes, two excavators and two generators were operated at ground level and four excavators were operated below ground level. No construction activity was conducted under Contract HK/2009/02 from 2300hrs on 14 November 2016 to 0700hrs on 15 November 2016. Total two generators were operated at ground level for lighting illumination of Portion 5.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to information provided by RSS, excavation works at Portion 5 was conducted under Contract HK/2009/02 at Portion 5 area (West of Wan Chai Ferry Pier) from 1900hrs to 2300hrs on 14 November 2016. Total two crawler cranes and two excavators were operated at ground level and four excavators were operated below ground level. Two generators were operated at ground level. Based on review on site information, relevant Construction Noise Permits GW-RS0593-15 for the above construction activities and above operation of the generators were confirmed in place. No construction activity was conducted under Contract HK/2009/02 from 2300hrs on 14 November 2016 to 0700hrs on 15 November 2016 and two generators were operated at ground level for lighting illumination of Portion 5. In view of the public concern, the Contractor of HK/2009/02 confirmed that the two generators for lighting power supply at ground level at Portion 5 area since 23 November 2016 to minimize the noise impact to the surroundings. In addition, the Contractor of HK/2009/02 was reminded to upkeep the site control system for construction works carried out during restricted hours and night time for Construction Noise Permit compliance and maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public. Also, the Contractor of HK/2009/02 was recommended to review the enhancement noise mitigation measure to be adopted for the generators deployed at ground level before 2300hrs to alleviate potential noise concern to the surroundings.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD ref: H08/RS/0003 0890-16 dated 07 December 2016	24 Nov 2016	A public complaint referred by EPD received by ET on 07 December 2016	Construction Site at Victoria Park	Noise emanated from the construction site at Victoria Park after 1900hrs.	A public complaint referred by EPD was received by ET on 07 December 2016 (Case Ref.: H08/RS/00030890-16). The complainant reported that Noise was emanated in the construction site near Victoria Park after 19:00 and caused nuisance to nearby sensitive receivers on 24 November 2016. ET confirmed with the Resident Site Staff that welding works for the tie-rod for the vertical blinding concrete was undertaken by the Contractor of HY/2010/08 at the construction site in the Victoria Park from 1900hrs to 2300hrs on 24 November 2016. Total 3 nos. of welding machines (electric), 3 nos. of water pumps (electric) and 1 no. of AquaSED were in operation. Based on the site records confirmed by RSS, welding works for the tie-rod for the vertical blinding concrete was undertaken by the Contractor of HY/2010/08 at the construction site in the Victoria Park from 1900hrs to 2300hrs on 24 November 2016. Total 3 nos. of welding machines (electric), 3 nos. of water pumps (electric) and 1 no. of AquaSED were in operation and relevant Construction Noise Permit GW-RS0930-16 was in place for the construction works conducted during the above concerned period. In addition, according to relevant site information confirmed by RSS, the welding machines, water pumps and AquaSED were connected to and powered by Hong Kong Electric power grid. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	Investigation report submitted to EPD on 16 December 2016. Under EPD review



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
complaint J	10 January 2017	A public complaint referred by EPD received by ET on 16 January 2017	Causeway Bay Typhoon Shelter	Construction work at the reclamation site in Causeway Bay Typhoon Shelter area (Under the Island Eastern Corridor) was found after1900hrs on 10 January 2017 and the concrete lorry mixer and concrete pump may not comply with the Construction Noise Permit	A public complaint referred by EPD was received by ET on 16 January 2017 (Case Ref.: H08/RS/00001175-17). The complainant reported that construction work at the reclamation site in Causeway Bay Typhoon Shelter area (Under the Island Eastern Corridor) was found after 1900hrs on 10 January 2017. The complainant reported that there were 3 concrete pumps and around 10 concrete lorry mixers operating at the above site during the said period which may not comply with the Construction Noise Permit. ET confirmed with the Resident Site Staff that concreting of tunnel structure was conducted under Contract HY/2010/08 at Temporary Reclamation Area TS3 between 1900hrs and 2000hrs on 10 January 2017. Total 3 nos. of Lorry Mounted Concrete Pumps and 6 nos. of Concrete Lorry Mixers were operated at TS3 while temporary noise barrier was provided for 2 nos. of the operating Lorry Mounted Concrete Pumps and 4 nos. of the operating Concrete Lorry Mixers. Total 1 no. of Concrete Lorry Mixer was at stand-by within TS3 Works area. Concreting of tunnel structure was conducted under Contract HY/2010/08 at Temporary Reclamation Area TS3 between 2000hrs and 2030hrs 10 January 2017.Total 2 nos. of Lorry Mounted Concrete Pump and 4 nos. of Concrete Lorry Mixers were operated at TS3 while temporary noise barrier was provided for 1 no. of the operating Lorry Mounted Concrete Pumps and 2 nos. of the operating Concrete Pumps and 3 nos. of the operating Concrete Pumps and 3 nos. of the operating Concrete Pumps and 3 nos. of Concrete Lorry Mixers. Total 1 no. of Concrete Lorry Mix	Interim investigation report submitted to EPD on 03 February 2017.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Concreting of tunnel structure was conducted under Contract HY/2010/08 at Temporary Reclamation Area TS3 between 2030hrs and 2300hrs 10 January 2017. Total 1 no. of Lorry Mounted Concrete Pump and 2 nos. of Concrete Lorry Mixers were operated at TS3.	
					Based on the site records confirmed by RSS, concreting of tunnel structure was conducted under Contract HY/2010/08 at Temporary Reclamation Area TS3 between 1900hrs and 2300hrs on 10 January 2017. From 1900hrs to 2000hrs, total 3 nos. of Lorry Mounted Concrete Pumps and 6 nos. of Concrete Lorry Mixers while temporary noise barrier was provided for 2 nos. of the operating Lorry Mounted Concrete Pumps and 4 nos. of the operating Concrete Lorry Mixers. Total 1 no. of Concrete Lorry Mixer was at standby within TS3 Works area.	
					From 2000hrs to 2030hrs, total 2 nos. of Lorry Mounted Concrete Pump and 4 nos. of Concrete Lorry Mixers were operated at TS3 while temporary noise barrier was provided for 1 no. of the operating Lorry Mounted Concrete Pumps and 2 nos. of the operating Concrete Lorry Mixers. Total 1 no. of Concrete Lorry Mixer was at stand- by within TS3 Works area.	
					From 2030hrs to 2300hrs, total 1 no. of Lorry Mounted Concrete Pump and 2 nos. of Concrete Lorry Mixers were operated at TS3.	
					Relevant Construction Noise Permit GW-RS1232- 16 (Corresponding PME Groups operated include Group M, Group K and Group H) was in place for the construction works conducted during the above concerned periods and based on RSS information, a designated personnel on-site was responsible for controlling and supervising the switching between PME Groups. Meanwhile, there	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					is no sufficient information to conclude if the concerned PME(s) (Concrete Lorry Mixer and Lorry Mounted Concrete Pump) deployed behind the temporary noise barrier provided were not visible to nearby sensitive receivers.	
					As multiple PME grouping under the Construction Noise Permit are involved, the Contractor of HY/2010/08 was reminded to strictly follow the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in strict compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
ICC complaint case (Ref: #2- 321884477 6) dated 23 December 2017	22 Dec 2016	ICC complaint case referred by RSS received by ET on 18 January 2017	Construction Site Gate Exit near Expo Drive East	No wheel washing from CEDD work site, no supervision from the Resident Site Staff, mud was dispersed on the road and flush to the communal drain by Chun Wo-China Railway JV HK/2009/02.	A public complaint regarding the subject matter on wheel washing referred by RSS was received by ET on 18 January 2017 (ICC Ref: #2- 3218844776). The complainant reported that no wheel washing from CEDD work site, no supervision from the Resident Site Staff, mud was dispersed on the road and flush to the communal drain by Chun Wo-China Railway JV HK/2009/02. ET confirmed with the Resident Site Staff that the concerned location was Site Exit Gate No. 6 at Expo Drive East operated and maintained under HK/2009/02 on 22 December 2016. Site measures including provision of wheel washing facility was implemented by the Contractor of HK/2009/02 on the concerned date.	Final investigation report issued on 23 January 2017.
					According to information provided by RSS, the concerned location was Site Exit Gate No. 6 at Expo Drive East operated and maintained under HK/2009/02 on 22 December 2016. In view of the environmental concern, remedial measures including i) instructing all workers to conduct wheel	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					washing within the designated location with collection pit to prevent overflow of washing effluent and ii) manual removal of dirt/silt by worker instead of water flushing in case of dirt/muddy trail found on road were implemented by the Contractor on 28 December 2016. Also, the Contractor of HK/2009/02 was further reminded by the WDII RSS to maintain proper wheel washing facilities at Gate No.6 and inspect regularly to ensure that all vehicles leaving the site to public roads are free of mud. Nevertheless, the Environmental Team further reminded the Contractor on 04 January 2017 that site measures including i) wheel washing operation shall be conducted at the designated location behind the backfall to avoid overflow of washing effluent onto public road ii) any silt/ soil deposited of the public road shall be cleared manually shall be strictly followed and relevant remedial actions were taken by the Contractor of HK/2009/02 on 04 January 2017. According to site inspection conducted on 17 January 2017, the concerned site exit Gate No.6 was maintained in proper condition, no silt/ mud deposition was observed on the public road and wheel washing was conducted by the Contractor of HK/2009/02 at the designated location within the construction site to avoid overflow of washing effluent onto nearby public road.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC complaint case (Ref: #2- 351203393 6) dated 20 February 2017	20 February 2017	ICC complaint case referred by RSS received by ET on 24 February 2017	Victoria Park Swimming Pool	Noise was emanated from the construction site near Victoria Park Swimming Pool between 2300hrs to 2400hrs in the past months and caused nuisance.	An ICC complaint referred by RSS was received by ET on 24 February 2017 (CASE#2-3512033936). The complainant reported that noise was emanated from the construction site near Victoria Park Swimming Pool between 2300hrs to 2400hrs in the past months and caused nuisance. ET confirmed with the Resident Site Staff that no works was conducted under Contract HY/2010/08 near Victoria Park Swimming Pool (Hing Fat Street) during the restricted hours (from 1900hrs to 0700hrs on the following day) from 21 December 2016 to 20 February 2017. No works was conducted under Contract HY/2010/08near Victoria Park Swimming Pool (Hing Fat Street) during the restricted hours (from 1900hrs to 0700hrs on the following day) from 21 December 2016 to 20 February 2017. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	Final Investigation Report issued on 02 March 2017 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC complaint case (Ref: #2- 351547483 1) dated 21 February 2017	21 February 2017	ICC complaint case referred by RSS received by ET on 24 February 2017	Construction Site near Victoria Park Swimming Park and Causeway Bay Typhoon Shelter	Noise was emanated from the construction site near Victoria Park Swimming Pool between 2300hrs to 2400hrs in the past months and caused nuisance.	An ICC complaint referred by RSS was received by ET on 24 February 2017 (CASE#2-3515474831). The complainant reported that noise was emanated from the construction site near Victoria Park Swimming Pool and Causeway Bay Typhoon Shelter between 1900hrs to 2400hrs in the past months and caused nuisance.	Final Investigation Report issued on 07 March 2017 and case closed.
					ET confirmed with the Resident Site Staff that concreting of tunnel structure at Temporary Reclamation Area TS3 were conducted under Contract HY/2010/08 between 1900hrs and 2300hrs on 13, 14, 15, 16 and 18 February 2017. Total 3 nos. of concrete pump and 6 nos. of concrete lorry mixers were operated.	
					Concreting of tunnel structure at Temporary Reclamation Area TS3 were conducted under Contract HY/2010/08 between 1900hrs and 2100hrs on 21 February 2017. Total 3 nos. of concrete pump and 6 nos. of concrete lorry mixers were operated. Concreting of tunnel structure at Zone C was conducted under Contract HY/2010/08 between 1900hrs to 2300hrs on 17 and 20	
					February 2017. Total 1 no. of concrete pump and 2 nos. of concrete mixers were operated. Bar bending at Zone C was conducted under Contract HY/2010/08 between 1900hrs to 2300hrs on 13, 14, 15, 16, 18 and 19 February 2017. Total 1 no. bar bender and cutter was operated. No works was conducted under Contract HY/2010/08 near Victoria Park Swimming Pool (Hing Fat Street)	
					during the restricted hours (from 1900hrs to 0700hrs on the following day) across the period from 13 February 2017 to 21 February 2017. Based on the site records confirmed by RSS, no works was conducted under Contract HY/2010/08	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					near Victoria Park Swimming Pool (Hing Fat Street) during the restricted hours (from 1900hrs to 0700hrs on the following day) from 13 February 2017 to 20 February 2017. Concreting of tunnel structure at Temporary Reclamation Area TS3 was conducted under Contract HY/2010/08 between 1900hrs and 2300hrs on 13, 14, 15, 16 and 18 February 2017 and total 3 nos. of concrete pumps and 6 nos. of concrete lorry mixers were operated. Concreting of tunnel structure at Temporary Reclamation Area TS3 were conducted under Contract HY/2010/08 between 1900hrs and 2100hrs on 21 February 2017 and total 3 nos. of concrete pump and 6 nos. of concrete lorry mixers were operated. Relevant Construction Noise Permit GW-RS0029-17 was in place while it is considered that there is no sufficient information to indicate whether the Powered Mechanical Equipment were deployed at the designed location stipulated under the relevant Construction Noise Permit with noise mitigation measures required.	
					Concreting of tunnel structure at Zone C was conducted under Contract HY/2010/08 between 1900hrs to 2300hrs on 17 and 20 February 2017. Total 1 no. of concrete pump and 2 nos. concrete mixers were operated. Bar bending at Zone C was conducted under Contract HY/2010/08 between 1900hrs to 2300hrs on 13, 14, 15, 16, 18 and 19 February 2017 and total 1 no. bar bender and cutter was operated. Relevant Construction Noise Permit GW-RS1366-13 was in place while it is considered that there is no sufficient information to indicate whether the Powered Mechanical Equipment were deployed at the designed location stipulated under the relevant Construction Noise Permit with noise mitigation measures required.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Nevertheless, further to the joint ad-hoc inspection conducted by the ET/IEC on 13 February 2017 during restricted hours (between 1900hrs to 2200hrs), concurrent operations of 4 nos. of concrete lorry trucks at the Southern Side of TS3 near Construction Site Entrance and concurrent operations of 2 nos. of concrete lorry pumps and 2 nos. of concrete lorry truck at Western and Northern Side of TS3 were observed while the temporary noise barrier provided for the concrete lorry pump and concrete lorry truck at the Northern Side of TS3 could not screen entirely the concrete lorry truck and concrete lorry pump (Located at Northern Side of TS3) from nearby sensitive receivers. Therefore, it is considered that the above operations observed could not follow the PME grouping requirement and the specific condition 3.d.4 under the relevant Construction Noise Permit. In view of the above, the Contractor of HY/2010/08 was advised to enhance the site supervision and strictly implement the site control system for construction works carried out during restricted hours to ensure the PMEs deployed strictly comply with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	



Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
			Nature of Complaint Noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.	An ICC complaint referred by RSS was received by ET on 27 February 2017 (CASE#2-3521097579). The complainant reported that noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene. ET confirmed with the Resident Site Staff that no construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017 and between 0000hrs to 0200hrs on 22 February 2017. No construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017. No construction work was conducted under HY/2010/08 at Zone C (Victoria Park Road) and Temporary Reclamation Area Zone between 0000hrs to 0200hrs on 21 February 2017. Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular	Status Final Investigation Report issued on 02 March 2017 and case closed.
				maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
	Complaint 22 February	Complaintand Received By22ICC complaintFebruarycase referred2017by RSSreceived by ETon 27 February	Complaintand Received ByComplainant22ICC complaint case referred by RSS received by ET on 27 FebruaryConstruction Site at Victoria Harbour near Victoria Park	Complaintand Received ByComplainant22 February 2017ICC complaint case referred by RSS received by ET on 27 February 2017Construction Site at Victoria Harbour near Victoria ParkNoise was emanated from the construction Site at Victoria Harbour near Victoria ParkVictoria Harbour out and the construction Site at victoria ParkNoise was emanated from the construction Site at Victoria Harbour near Victoria ParkComplaint on 27 February 2017Construction Site at Victoria ParkConcrete Lorry wasConcrete Lorry was	Complaintand Received ByComplainant22 2017ICC complaint case referred by RSS received by ET on 27 February 2017Construction Site at Victoria ParkNoise was emanated from the construction near Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.An ICC complaint referred by RSS was received by ET on 27 February 2017 (CASE#2-3521097579). The complainant reported that noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.An ICC complaint referred by RSS was received by ET on 27 February 2017 (CASE#2-3521097579). The complainant reported that noise was emanated from the construction Site at Victoria Harbour near Victoria Park from 0000hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.20172017Site at Victoria Park Park Road)An ICC complaint referred by RSS was received by ET on 0200hrs to 0200hrs on Tuesday and caused nuisance and Concrete Lorry was observed on scene.ET confirmed with the Resident Site Staff that no construction work was conducted under



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC Complaint Case (CASE #2- 357615753 8 dated 05 March 2017)	05 March 2017	ICC complaint referred by RSS was received by ET on 06 March 2017	Construction works area under Contract HK/2009/02 for Wanchai Development Phase II	Noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.	An ICC complaint referred by RSS was received by ET on 06 March 2017 (CASE#2-3576157538). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.	Investigation report issued on 10 March 2017 and case closed.
2017)					ET confirmed with the Resident Site Staff that no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level.	
					Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 no. of loader were in operation below ground level.	
					According to the information confirmed by RSS, no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4	
					(Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 loader were in operation below	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					ground level. Relevant Construction Noise Permit GW-RS1305-16 was in place.	
					Nevertheless, in view of the public concern, the Contractor of HK/2009/02 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HK/2009/02 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
EPD complaint (Case Ref: H05/RS/00 06240-17)	05 March 2017	EPD complaint referred by RSS was received by ET on 14 March 2017. EPD clarified the complaint case shall be was referred by ICC Complaint Hotline (CASE #2- 3576157538)	Construction works area under Contract HK/2009/02 for Wanchai Development Phase II	Noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected.	A EPD complaint was referred to the ET on 14 March 2017 (CASE Ref: H05/RS/0006240-17). The complainant reported that noise was emanated from the construction works under Contract HK/2009/02 for Wanchai Development Phase II on 05 March 2017 and potential violation of ordinance was suspected. ET confirmed with the Resident Site Staff that no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 no. of loader were in operation below ground level.	Interim Investigation report issued on 10 March 2017 and case closed. EPD advised no comment on 09 Oct 2017 on the interim report submitted and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					According to the information confirmed by RSS, no works was conducted under Contract HK/2009/02 from 0000hrs to 0830hrs on 05 March 2017. Removal ELS waling at Portion 5 (West of WanChai Ferry Pier) was conducted under Contract HK/2009/02 from 0830hrs to 1700hrs on 05 March 2017. Total 2 nos. of crawler cranes were in operation at ground level. Tunnel backfilling and construction of temporary walls at Portions 3&4 (Near Wan Shing Street) were conducted under Contract HK/2009/02 from 0830hrs to 1700hrs. Total 1 no. of excavator and 1 no. of dump truck were in operation at ground level and 2 nos. of excavator and 1 loader were in operation below ground level. Relevant Construction Noise Permit GW-RS1305-16 was in place. Nevertheless, in view of the public concern, the Contractor of HK/2009/02 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HK/2009/02 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
ICC complaint Case (CASE#2- 360318289 0) dated 10 March 2017	10 March 2017	An ICC complaint referred by RSS was received by ET on 13 March 2017	Construction Site at Victoria Park	Noise was emanated from the construction Site at Victoria Park from 2300hrs to 2400hrs on 10 March 2017 and caused nuisance to nearby residents.	An ICC complaint referred by RSS was received by ET on 13 March 2017 (CASE#2-3603182890). The complainant reported that noise was emanated from the construction Site at Victoria Park from 2300hrs to 2400hrs on 10 March 2017 and caused nuisance to nearby residents. ET confirmed with the Resident Site Staff that no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.	Investigation Report issued on 15 March 2017 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Based on the information provided by the RSS, no construction work was conducted under Contract HY/2010/08 at Victoria Park at from 2300hrs to 2400hrs on 10 March 2017.	
					Nevertheless, in view of the public concern, the Contractor of HY/2010/08 was reminded to maintain the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit. The Contractor of HY/2010/08 was also reminded to maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
EPD complaint Case (CASE Ref: H05/RS/00 014415- 17(14448- 17) dated 18 May 2017	11 May 2017	An EPD complaint referred to ET on 18 May 2017	Construction Site under Contract HK/2009/02	Construction work was found on 10 May 2017 (~03:52) that caused noise nuisance. According to the information provided by the IEC on 11 May 2017 and 15 May 2017, it was alleged that the concreting work under Contract No. HK/2009/02 was carried out for the Central-Wan Chai Bypass Top Slab Bay 6 during night time on 09 May 2017 and early morning on 10 May 2017 (between 11:00pm on 09 May 2017 and about 04:00 a.m. on 10 May 2017) with 3 pump trucks, 10 vibrating pokers, 9 concrete trucks and 2 generators in operation.	An EPD complaint was referred to the ET on 18 May 2017 (CASE Ref: H05/RS/00014415- 17(14448-17). The complainant reported that: Construction work was found on 10 May 2017 (~03:52) that caused noise nuisance. According to the photos provided by the complainant lorry mounted concrete pump were used. According to the information provided by the IEC on 11 May 2017 and 15 May 2017, it was alleged that the concreting work under Contract No. HK/2009/02 was carried out for the Central-Wan Chai Bypass Top Slab Bay 6 during night time on 09 May 2017 and early morning on 10 May 2017 (between 11:00pm on 09 May 2017 and about 04:00 a.m. on 10 May 2017) with 3 pump trucks, 10 vibrating pokers, 9 concrete trucks and 2 generators in operation. The concreting works under Contract No. CEDD HK/2009/02 was also carried out for the Central – Wan Chai Bypass Bay 10A OHVS Slab after 23:00 on 12 May 2017 (after 23:00) with 1 Pump truck, 2 vibrating pokers, 1 concrete trucks and 3 generators in operation.	Interim Investigation report submitted to EPD on 26 May 2017. EPD advised no comment on 09 Oct 2017 on the interim report submitted and case closed



Complaint Log No. (Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				The concreting works under Contract No. CEDD HK/2009/02 was also carried out for the Central – Wan Chai Bypass Bay 10A OHVS Slab after 23:00 on 12 May 2017 (after 23:00) with 1 Pump truck, 2 vibrating pokers, 1 concrete trucks and 3 generators in operation.	ET confirmed with the Resident Site Staff that 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017. 2 nos. of vibratory pokers, 1 no. of concrete truck, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017. According to the RSS site information, 10 nos. of vibratory pokers, 3 nos. of concrete pump trucks and 3 nos. of generator were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 09 May 2017 to 0408hrs on 10 May 2017 while 9 nos. of concrete trucks were in operation at around 0320hrs on 10 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 11 May 2017, ad-hoc inspection was conducted by the Environmental Team on 13 May 2017 around 00:40 hrs. No construction operation and no PME deployment was observed at the time of inspection. According to the RSS site information, 2 nos. of vibratory pokers, 1 no. of concrete pump truck, and 3 nos. of generators were in operation at Tunnel Portion 5, Top Slab 6 from 2300hrs on 12 May 2017 to 2340hrs on 12 May 2017 and could not comply with the item 3a - PME requirement under Construction Noise Permit GW-RS1297-16. In response to the information provided by the RSS/ IEC on 15 May 2017, ad-hoc inspection was conducted by the Environmental Team on 19 May	



2017 around 22:20trs: 2 nos. of concrete truck, 1 no. of concrete pump tuck were observed in operation at the time of inspection and relevant CNP GW-R80334-17 was in place. Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction Noise Permit normaliance including i) fully review Construction Noise Permit compliance with relevant Construction Noise Permit compliance with relevant Construction Noise Permit compliance with relevant Construction Noise Permit and iii) review the construction soles never the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction operations and PME are operated in accordance to relevant Construction Noise Period within the specified allowable period. The Construction operations and PME are operated in accordance to relevant Construction Noise recommended to provide briefing and training section to site staffs to enhance the site awareness and understanding on relevant construction noise requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/209/02 during restricted hours and report relevant findings, if any, accordingly.	Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
						2017 around 22:20hrs. 2 nos. of concrete truck, 1 no. of concrete pump tuck were observed in operation at the time of inspection and relevant CNP GW-RS0334-17 was in place. Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction operations and PME are operated in accordance to relevant Construction Noise Period. The Contractor of HK/2009/02 is also recommended to provide briefing and training section to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours. The ET/IEC/RSS will maintain ad hoc checking on the construction operations under Contract HK/2009/02 during restricted hours and report	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD complaint Case (CASE Ref: N/A) dated 23 May 2017	23 May 2017	An EPD complaint referred to ET on 25 May 2017	Construction Site under Contract HK/2009/02	Concreting works under Contract No. CEDD HK/2009/02 was carried out with crawler cranes, 10-12 vibratory pokers, and 7 concrete lorry mixers in the morning on 21 May 2017 without a valid CNP. Also, at 15:30 on 21 May 2017, 9 vibratory pokers and 7 concrete lorry mixers were observed in operation. These works were suspected to contravene the Noise Control Ordinance (NCO).	An EPD complaint was referred to the ET on 25 May 2017 (CASE Ref: N/A). The complainant reported that concreting works under Contract No. CEDD HK/2009/02 was carried out with crawler cranes, 10-12 vibratory pokers, and 7 concrete lorry mixers in the morning on 21 May 2017 without a valid CNP. Also, at 15:30 on 21 May 2017, 9 vibratory pokers and 7 concrete lorry mixers were observed in operation. These works were suspected to contravene the Noise Control Ordinance (NCO). ET confirmed with the Resident Site Staff that 12 nos. of vibratory pokers were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs on 21 May 2017. 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017. 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs on 21 May 2017. 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs on 21 May 2017. 7 nos. of concreting trucks were operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017. According to the RSS site information, the following PMEs were operated at Tunnel Portion 5 from 0915hrs to 1030hrs to 1740hrs; ii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0800hrs to 0915hrs; iii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0730hrs to 1740hrs; ii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0730hrs to 1740hrs; iii) 3 nos. of crawler cranes were operated at Tunnel Portion 5 from 0730hrs to 1650hrs; v) 4 nos. of generators were operated at Tunnel Portion 5 from 0915hrs to 1030hrs on 21 May 2017; iv) 4 nos. of concrete pump trucks were operated at Tunnel Portion 5 from 0750hrs to 1650hrs; v) 4 nos. of generators were operated at Tunnel Portion 5 from 0730hrs to 1740hrs ;) 7 nos. of concreting trucks were	Investigation report submitted to EPD on 02 June 2017. EPD advised no comment on 09 Oct 2017 on the interim report submitted and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					operated at intervals between the time period of 0730hrs to 1740hrs on 21 May 2017 and the above construction operations could not comply with the item 3a - PME requirement under the Construction Noise Permit GW-RS334-17.	
					EPD notification on the cancellation of the Construction Noise Permits GW-RS0334-17 and Construction Noise Permit GW-RS1297-16 was received by the Environmental Team on 26 May 2017. Ad hoc inspection was conducted by the Environmental Team on 26 May 2017 around 2230hrs and on 28 May 2017 around 1520hrs and no construction works and no operation of PME was observed at the concerned site Portion 5 at the time of inspections. Notwithstanding the above, in view of the identified non-conformance, the Contractor of HK/2009/02 was requested to implement the following rectification measures to ensure the strict construction noise permit compliance including i) fully review Construction Noise Permit in force and the tentative construction operations to ensure the strict Construction Noise Permit compliance under Noise Control Ordinance, ii) fully review the site control system for construction works carried out during restricted hours to ensure the Construction Noise Permit and iii) review the construction sequence and schedule to ensure the construction sequence and schedule to provide briefing and training section to site staffs to enhance the site awareness and understanding on relevant construction noise permit(s) requirement during restricted hours.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Nature of Complaint Construction work from a construction site near Renaissance Hong Kong Harbour View Hotel was found around 2315 hrs on 26 June 2017, causing noise nuisance.	OutcomeAn EPD complaint was referred to the ET on 13July 2017 (CASE Ref: H05/RS/00021311-17). Thecomplainant reported that construction work from aconstruction site near Renaissance Hong KongHarbour View Hotel was found around 2315 hrs on26 June 2017, causing noise nuisance.ET confirmed with the Resident Site Staff thatManual re-bar fixing works was carried out underContract HK/2009/02 from 2300hrs to 2330hrs on26 June 2017 at Portion 5 Bay 15 (Non -Designated Area) top slab area adjacent to thecovered walkway of the Wan Chai Ferry Pier. 1 no.of generator was operated at ground level and 2nos. of generators were operated below groundlevel from 2300hrs to 2400hrs on 26 June 2017. Inaddition 16 electric water pump were operatedbelow ground level from 2300hrs to 2400hrs on 26 June 2017.Notwithstanding the information stated in aboveitem 1), according to relevant Resident Site Staffsite record, it was recorded that 1 no. of mobilecrane and 1 no. of bar bender were deployed andoperated at Portion 5 area (West of Wan ChaiFerry Pier) under Contract HK/2009/02 after2300hrs on 26 July 2017. Upon warning given byWDII Resident Site staff to the Contractor ofHK/2009/02, the operation of crawler crane forlifting rebar and operation of bar bender machinewere suspended at around 2315hrs on 26 June2017.No construction activity and site operation wascarried out under Contract HK/2009/01 from	Status Interim investigation report submitted to EPD on 21 July 2017. EPD advised no comment on 09 Oct 2017 on the interim report submitted and case closed
					2300hrs to 2400hrs on 26 June 2017. According to the RSS site information, manual re- bar fixing works was carried out under Contract HK/2009/02 from 2300hrs to 2330hrs on 26 June 2017 at Portion 5 Bay 15 (Non - Designated Area)	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					top slab area adjacent to the covered walkway of the Wan Chai Ferry Pier. 1 no. of generator was operated at ground level and 2 nos. of generators were operated below ground level from 2300hrs to 2400hrs on 26 June 2017 while 16 electric water pump were operated below ground level at Portion 5 Bay from 2300hrs to 2400hrs on 26 June 2017 and the relevant Construction Noise Permit GW- RS0527-17 for the above operation was in place. However, site record on the model of generators deployed on the concerned night was not available.	
					Notwithstanding the above, according to relevant Resident Site Staff site record, it was recorded that 1 no. of mobile crane and 1 no. of bar bender machine were deployed and operated at Portion 5 area (West of Wan Chai Ferry Pier) under Contract HK/2009/02 after 2300hrs on 26 July 2017 without a valid Construction Noise Permit. Upon warning given by WDII Resident Site staff to the Contractor of HK/2009/02, the operation of crawler crane for lifting rebar and operation of bar bender machine were suspended at around 2315hrs on 26 June 2017. According to Contractor of HK/2009/02, the operation bar bender machine was suspended upon warning by RSS team and the operation of crawler crane was suspended upon moving to a proper location to avoid obstruction for next day work.	
					Meanwhile, no construction activity and site operation was carried out under Contract HK/2009/01 from 2300hrs to 2400hrs on 26 June 2017. In view of the above operation of powered mechanical equipment under Contract HK/2009/02 beyond 2300hrs, the Contractor of HK/2009/02 was required and urged to implement the following	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					remedial measures to ensure the strict construction noise permit compliance including:- Fully review the site control system for	
					construction works carried out during restricted hours, in particular to ensure the frontline supervisors responsible for restricted hours construction operations are trained with comprehensive understanding on the requirement of the Construction Noise Permit in force to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit.	
					To assign delegated and competent personnel on- site to conduct checking on the deployment of PMEs on-site prior and during restricted hours to ensure only PMEs allowed under relevant Construction Noise Permit would be operated.	
					In addition, the following preventive measures are also recommended including the Contractor of HK/2009/02 is recommended to provide regular briefing and training section to site staffs and frontline workers to enhance the workers awareness and understanding on relevant Construction Noise Permit(s) requirement during restricted hours.	
					The Contractor of HK/2009/02 is recommended to review the construction operation planning procedures to ensure relevant PME(s) required for conducting the planned operation to ensure required PME are adequate considered and covered by relevant Construction Noise Permit.	
					In view of the recent concern over restricted hours construction operations, a meeting was held amongst the CEDD, the RSS team, the Contractor of HK/2009/02 and the Environmental Team on 21 July 2017 to review the site control measures and enhancement measures to be adopted for restricted hours construction operations control for	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Construction Noise Permit Compliance. A detailed implementation plan would be prepared by the Contractor of HK/2009/02 and further supplemented.	
EPD complaint Case (CASE Ref: H05/RS/00 022136-17) dated 17 July 2017 ICC complaint case (Ref: 2- 412202158 9) dated 14 July 2017	14 July 2017	EPD complaint referred to ET on 17 July 2017 ICC complaint referred to ET on 25 July 2017	Island Eastern Corridor near Provident Centre	Night time construction noise emanated from construction works conducted during early hours of 14 July 2017 at Island Eastern Corridor near Provident Centre.	 An EPD complaint was referred to the ET on 17 July 2017 (CASE Ref: H05/RS/00022136-17). The complainant reported that night time construction noise emanated from construction works conducted during early hours of 14 July 2017 at Island Eastern Corridor near Provident Centre. An ICC complaint case (Ref: 2-4122021589) was Referred to the ET on 25 July 2017. The complainant reported that the workers are now doing extremely noisy works at the Island Eastern Corridor near Provident Centre affecting the nearby residents. As the ICC complaint case refers to the noise concern at the same location at the same hours on the same date, hence the ICC case is considered as the same complaint case under the EPD complaint for investigation purpose. ET confirmed with the Resident Site Staff that emergency road repairing work including the repairing of movement joint at Pier 46 and three potholes along IEC Westbound was carried out under Contract HY/2009/19 around the concerned location from 0000hrs to 0600hrs on 14 July 2017. Total 1 no. of hand held breaker and 1 no. of hand held drill for grout mixing were operated. According to the RSS site information, emergency road repairing work including the repairing of movement joint at Pier 46 and three potholes along IEC Westbound was carried out under Contract HY/2009/19 around the concerned location from 0000hrs to 0600hrs on 14 July 2017. Total 1 no. of hand held breaker and 1 no. of hand held drill for grout mixing were operated. 	Interim report submitted to the EPD on 25 July 2017. EPD advised on 20 Jun 2018 no comment on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Nature of Complaint	Outcome 0000hrs to 0600hrs on 14 July 2017. Total 1 no. of hand held breaker and 1 no. of hand held drill for grout mixing were operated. A written advance notification was issued to the EPD on 13 July 2017 regarding the aforesaid emergency road repairing works. In view of the public concern, the Contractor of HY/2009/19 is recommended to adopt additional noise mitigation measure for future emergency road repairing works, if any, at night time hours around the concerned location. In response to the public concern, the Contractor of HY/2009/19 would adopt the following additional measures for future emergency road repairing works including: i) For any emergency works requiring, for example, breaking or any other noisy activities, wherever possible, temporary noise barrier or acoustic mat will be use to fence of the line of sight between the noise emanating source and the NSR, ii) Covering breaking head with acoustic mat to minimize noise if breaking would be conducted and iii) complete noisy work as soon as possible to minimize disturbance to the nearby residents.	Status



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD complaint Case (CASE Ref: H05/RS/00 022835-17) dated 21 July 2017	20 July 2017	EPD complaint referred to ET on 21 July 2017	Construction site near Renaissance Hong Kong Harbour View Hotel and Wanchai Pier	Mechanical noise was emanated from a construction site near Renaissance Hong Kong Harbour View Hotel and Wanchai Pier from late night till dawn recently, causing noise nuisance.	An EPD complaint was referred to the ET on 21 July 2017 (CASE Ref: H05/RS/00022835-17). The complainant reported that mechanical noise was emanated from a construction site near Renaissance Hong Kong Harbour View Hotel and Wanchai Pier from late night till dawn recently, causing noise nuisance. ET confirmed with the Resident Site Staff that unloading of fill material was conducted under Contract HK/2009/02 at WCR3 area (West of Wan Chai Ferry Pier) from 2300hrs on 19 July 2017 to 0540hrs on 20 July 2017. 1 no. of grab dredger was operated for the above construction works. No construction activities or site operation was conducted under Contract HK/2009/01 from 2300hrs on 19 July 2019 to 0700hrs on 20 July 2017. According to the RSS site information, unloading of fill material was conducted under Contract HK/2009/02 at WCR3 area (West of Wan Chai Ferry Pier) from 2300hrs on 19 July 2017 to 0540hrs on 20 July 2017. 1 no. of grab dredger was operated for the above construction works and relevant Construction Noise Permit GW-RS0348-17 was in place and noise barrier with surface mass density of not less than 5kg/m2 was provided to the power generating part of the grab dredger operated from 2300hrs on 19 July 2017 to 0540hrs on 20 July 2017. Meanwhile, no construction activities or site operation was conducted under Contract HK/2009/01 from 2300hrs on 19 July 2019 to 0700hrs on 20 July 2017.	Interim report submitted to EPD on 26 July 2017. EPD advised no comment on 09 Oct 2017 on the interim report submitted and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					control system for construction works carried out during restricted hours and night time for Construction Noise Permit compliance and maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
ICC complaint Case (CASE Ref: #2- 416246715 1) dated 25 July 2017	25 July 2017	ICC complaint referred to ET on 26 July 2017	CEDD Construction Site near Wanchai Ferry Pier	No watering system was provided to the excavation works conducted at a CEDD Construction Site near Wanchai Ferry Pier resulting in dust impact to the public area beyond site hoarding.	An ICC complaint was referred to the ET on 26 July 2017 (CASE Ref: #2-4162467151). The complainant reported that no watering system was provided to the excavation works conducted at a CEDD Construction Site near Wanchai Ferry Pier resulting in dust impact to the public area beyond site hoarding. ET confirmed with the Resident Site Staff that breaking works and backfilling works were conducted under Contract HK/2009/02 at the concerned location on 25 July 2017 afternoon. Dust mitigation measures including water spraying was implemented for the above construction activities on 25 July 2017 at the concerned location. According to the RSS site information, breaking works and backfilling works were conducted under Contract HK/2009/02 at the concerned location on 25 July 2017 afternoon while dust mitigation measures including water spraying was implemented for the above construction activities on 25 July 2017 at the concerned location on 25 July 2017 afternoon while dust mitigation measures including water spraying was implemented for the above construction activities on 25 July 2017 at the concerned location. During Environmental Team ad hoc inspection conducted on 26 July 2017, water spraying was found	Investigation report issued on 04 August 2017 and case closed.
					insufficient to mitigate the extended area of breaking operation and construction dust impact to surroundings public area was observed.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Subsequently, Contractor of HK/2009/02 was reminded to enhance the dust suppression measure for the dust generating works.	
					In response to the observed environmental concern, the Contractor of HK/2009/02 has strengthened the water spraying coverage to all breaking operation area and haul road to minimize the potential dust impact. Follow up inspection was conducted by Environmental Team on 27 July 2017 and no further dust impact was observed.	
EPD complaint Case (CASE Ref: N/A) dated 06 September 2017	24 August 2017	EPD complaint referred to ET on 06 September 2017	Portion 5 (West of Wanchai Ferry Pier) under Contract HK/2009/02	Site inspection record regarding improper dust suppression measure during excavation	EPD complaint regarding the inspection report issued by the EPD on 24 August 2017 on improper dust suppression measure during excavation was referred to the ET on 06 September 2017. As clarified with the EPD, the concerned location of the observation refers to Portion 5 (West of Wanchai Ferry Pier). ET confirmed with the Resident Site Staff that backfilling and compaction works were conducted under Contract HK/2009/02 for CWB Tunnel at the concerned location at Portion 5 (West of Wanchai Ferry Pier). According to RSS information, dust suppression measures including water spraying for stockpile stored on site was generally implemented by the Contractor of HK/2009/02 while it was observed and considered that the extent of water spraying was insufficient on 24 August 2017 at the aforesaid location.	Investigation report issued on 15 September 2017. EPD advised no comment on 09 Oct 2017 on the interim report submitted and case closed
					Follow up inspection was conducted by the Environmental Team on 08 September 2017. Concerned stockpile of dusty materials at the concerned location at Portion 5 was observed removed from site and mitigation measure including compaction and water spraying for exposed soil surface at Portion 5 were implemented and no particular dust impact was	



		observed at the concerned location at Portion 5. Subsequent follow up inspection was conducted by the Environmental Team on 11 September 2017. Exposed surface at construction site area Portion 5 was observed compacted and partially maintained in dampened condition. Despite no particular dust impact was observed, the Contractor of HK/2009/02 was further advised to review the site condition and adequately implement the following construction dust mitigation measures, as appropriate, to avoid potential dust impact to the surroundings:-	
		Exposed earth shall be properly treated by compaction, turfing, hydro seeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within 6 months after the last construction activity on the construction site or part of the construction site where the exposed earth lies to avoid potential dust impact; Stockpile of dusty materials, if any, shall be either covered entirely by impervious sheeting; or placed in an area sheltered on the top and the 3 sides; or sprayed with water or a dust suppression chemical so as to maintain the entire surface wet and; Construction site surface with dusty materials should be sprayed with water to maintain entire surface wet to avoid potential dust impact to the surroundings.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
ICC complaint Case (CASE Ref: #2- 424207350 5) dated 18 September 2017	18 Septemb er 2017	ICC complaint referred to ET on 19 September 2017	A section of Island East Corridor opposite to Victoria Park	On recent Sundays during midnight hours, noise were emanated from road construction works and excavators for consecutive hours without any noise mitigation measures.	ICC complaint referred by RSS was received by ET on 19 September 2017 (CASE#2- 4242073505). The complainant reported that on recent Sundays during midnight hours, noise were emanated from road construction works and excavators for consecutive hours without any noise mitigation measures. ET confirmed with the Resident Site Staff that Reinstatement of movement joint at Island East Corridor Westbound Carriageway was conducted under Contract HY/2010/08 between 0000hrs to 0700hrs on 10 September 2017(Sunday) and 17 September 2017(Sunday). Powered Mechanical Equipment (PME) including 2 nos. of electric breakers, 2 nos. of portable generator, 1 no. of saw cut machine, 2 nos. of grab lorry, 1 no. of mini concrete mixer, 1 no. of welding set and 1 no. of poker vibrator were deployed in separate groups between 0000hrs to 0700hrs on 10 September 2017 and 17 September 2017. Amongst the above, 2 nos. of electric breakers and 1 no. of saw cut machine were operated only between 0000hrs to 0200hrs and 1 no. of poker vibrator was only operated beyond 0600hrs. Noise Mitigation measure including acoustic enclosure were provided locally for the use of electric breaker, portable generator and saw cut machine between 0000hrs to 0700hrs on 10 September 2017 and 17 September 2017.	Final Investigation report issued on 30 September 2017 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					September 2017(Sunday). Powered mechanical equipment (PME) including 2 nos. of electric breakers, 2 nos. of portable generator, 1 no. of saw cut machine, 2 nos. of grab lorry, 1 no. of mini concrete mixer, 1 no. of welding set and 1 no. of poker vibrator were deployed in separate PME groups between 0000hrs to 0700hrs on 10 September 2017 and 17 September 2017. Amongst the above, 2 nos. of electric breakers and 1 no. of saw cut machine were operated only between 0000hrs to 0200hrs and 1 no. of poker vibrator was only operated beyond 0600hrs on 10 and 17 September 2017. Noise Mitigation measure including acoustic enclosure were provided locally for the use of electric breaker, portable generator and saw cut machine between 0000hrs to 0700hrs on 10 September 2017 and 17 September 2017.	
					Based on the site information, the aforesaid PMEs were deployed under the Construction Noise Permit GW-RS0697-17 while it was found the PMEs were deployed beyond the specified area under the Construction Noise Permit GW-RS0697-17. It was further found that operation of grab lorry for the removal of concrete debris was conducted beyond the specified period allowed under condition 4.d.2 of Construction Noise Permit GW-RS0697-17. Additionally, based on the site layout and the operation location of 2 nos. of electric breakers, it is considered that the operation of the two electric hand held breakers could not fulfil the condition 3.d.7. under Construction Noise Permit GW-RS0697-17.	
					In view of the above findings, the Contractor of HY/2010/08 was requested to immediately	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					implement the following rectification measures to ensure the strict compliance with the Noise Control Ordinance including i) Critically review the Construction Noise Permit(s) in force and renew the Construction Noise Permit(s), if necessary, for the tentative construction operations to ensure the strict compliance with the Construction Noise Permit under Noise Control Ordinance, ii) Review the site control system for construction works carried out during restricted hours to ensure the PMEs deployed are in compliance with relevant Construction Noise Permit and iii) Fully review the construction method, sequence and schedule to ensure the construction operations and associated PMEs are operated within the specified allowable period in accordance with the relevant Construction Noise Permit.	
ICC complaint (CASE Ref: #2- 4320996036) dated 08 November 2017	08 Novemb er 2017	An ICC complaint was referred by RSS to the ET on 13 November 2017	Construction works area opposite to City Garden Block 9	Noise was emanated from construction works during morning hours from 0300hrs to 0500hrs and metal hammering noise was still emanated at night time	An ICC complaint was referred by RSS to the ET on 13 November 2017 (CASE Ref: #2-4320996036). The complainant reported that noise was emanated from construction works conducted opposite to City Garden Block 9 during morning hours from 0300hrs to 0500hrs and metal hammering noise was still emanated at night time causing nuisance to nearby residence. ET confirmed with the Resident Site Staff that night work including nut fixing works for post supporting bracket of noise enclosure was conducted under Contract HY/2009/19 at IECL westbound bridge Pier 40 around the concerned location from 0300hrs to 0500 hrs on 07 November 2017. Crane lorry for panel removal and hand tools for fixing of nuts were deployed with relevant Construction Noise Permit GW-RS0837-17. No construction works was conducted under Contract HY/2009/19 from 1900hrs to 2300hrs on 07 November 2017. Night work including nut fixing works for post supporting bracket of noise enclosure was conducted under Contract HY/2009/19 at IECL westbound bridge Pier 38 around the concerned location from 0300hrs to 0500hrs on 08 November 2017. Crane lorry for panel removal and hand tools for fixing of nuts were deployed	Investigation Report issued on 23 November 2017 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					with relevant Construction Noise Permit GW-RS0837-17. Night work including nut fixing works for post supporting bracket of noise enclosure was conducted under Contract HY/2009/19 at IECL westbound bridge Pier 40 around the concerned location from 0300hrs to 0500 hrs on 07 November 2017. Crane lorry for panel removal and hand tools for fixing of nuts were deployed. Night work including nut fixing works for post supporting bracket of noise enclosure was conducted under Contract HY/2009/19 at IECL westbound bridge Pier 38 around the concerned location from 0300hrs to 0500hrs on 08 November 2017 and crane lorry for panel removal and hand tools for fixing of nuts were deployed. Relevant Construction Noise Permit GW-RS0837-17 was in placed for the above construction activities conducted under Contract HY/2009/19 outside the Designated Area zone under Noise Control Ordinance. No construction works was conducted under Contract HY/2009/19 from 1900hrs to 2300hrs on 07 November 2017. In view of the public concern, the Contractor of HY/2009/19 is recommended to adopt soft face hammer to minimize potential noise emanation during works and ii) minimize potential bumping sound with the ground by good practice of HY/2009/19 was further reminded to observe and strictly follow condition 3.d.7 under relevant Construction Noise Permit GW-RS0837-17.	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD complaint (Case ref: H08/RS/0003 7826-17) dated 24 November 2017	21 November 2017	An EPD complaint (Case ref: H08/RS/0003782 6-17) referred to the ET on 24 November 2017	North Point New Reclamation Area, Oil Street, North Point.	Noise was emanated from construction works conducted at around 2200hrs	An EPD complaint (Case ref: H08/RS/00037826-17) was referred to the ET on 24 November 2017. The complainant reported that noise was emanated from construction works conducted at around 2200hrs at North Point New Reclamation Area, Oil Street, North Point. ET confirmed with the Resident Site Staff that welding works to the steel strut at Approach Ramp Phase 2 Portion X) were conducted under Contract HY/2009/19 on 20 November 2017 and total 3 nos. of welding machines were operated until 2130hrs. No works was conducted between 2130hrs to 2230hrs on 20 November 2017. No construction works was conducted under HY/2011/08 on 20 November 2017 between 2130hrs to 2230hrs. Welding works to the steel strut at Approach Ramp Phase 2 (Portion X) were conducted under Contract HY/2009/19 on 20 November 2017 and total 3 nos. of welding machines were operated until 2130hrs. No works was conducted between 2130hrs to 2230hrs on 20 November 2017. Meanwhile, no construction works was conducted under HY/2011/08 on 20 November 2017 between 2130hrs to 2230hrs. Nevertheless, the Contractor of HY/2011/08 and the Contractor of HY/2009/19 were reminded to maintain proper site control and all construction activities to be conducted during restricted hours shall follow relevant Construction Noise Permit.	Interim investigation report submitted to EPD on 08 December 2017. EPD advised on 08 Jan 2018 no comment on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD complaint (H05/RS/397 21-17) dated 15 December 2017	08 December 2017	An EPD complaint (Case Ref: H05/RS/39721- 17) referred to ET on 15 December 2017	Construction site near the HKCEC and Wanchai Pier	Construction dust was generated from rock breaking activities of a construction site	An EPD complaint was referred to the ET on 14 December 2017 (CASE Ref: H05/RS/39721-17). The complainant reported that construction dust was generated from rock breaking activities of a construction site near the HKCEC and Wanchai Pier on 08 December 2017 (0815hrs), causing nuisance. ET confirmed with the Resident Site Staff that breaking works and backfilling works were conducted under Contract HK/2009/02 at Portion 5 (Site Area near Wanchai Ferry Pier) on 08 December 2017 around 0815hrs and mitigation measure including water spraying was provided for the breaking works. According to the RSS site information, breaking works. According to the RSS site information, breaking works. According to the RSS site information was provided for the breaking works. Follow up inspection was conducted on 19 December 2017, ground Compaction and intermittent breaking works was observed while dust suppression was observed implemented at intervals under Contractor of HK/2009/02 while no particular dust emission was observed from the above works. Nevertheless, in view of the public concern, the Contractor of HK/2009/02 was reminded that adequate dust suppression measure shall be provided for breaking works and dusty surface to avoid dust emission and minimize any potential dust impact to the surroundings. The Contractor of HK/2009/02 is also recommended to arrange the breaking works, if any, to be conducted collectively at specified location to enhance the overall site control and effectiveness of dust suppression measure. The Contractor is also recommended to arrange the breaking works, if any, to be conducted collectively at specified location to enhance the overall site control and effectiveness of dust suppression effectiveness.	Interim investigation report submitted to EPD on 21 December 2017. EPD advised on 08 Jan 2018 no comment on the interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD complaint (H08/RS/000 00972-18) dated 11 January 2018	08 January 2018	An EPD complaint (Case Ref: H08/RS/0000097 2-18) referred to ET on 11 January 2018	North Point new Reclamation Area. Oil Street	Night time construction noise after 7pm	 An EPD complaint (Case ref: H08/RS/00000972-18) was referred to the ET on 11 January 2018. The complainant reported that night time construction noise after 7 pm near North Point New Reclamation Area, Oil Street, North Point. ET confirmed with the Resident Site Staff that no construction works was conducted under Contract HY/2011/08 on 08 January 2018 from 1900hrs to 2300hrs at the concerned location. Concreting operation was conducted under Contract HY/2009/19 at Approach Ramp Phase 2 site area at Oil Street on 08 january 2018 from 1900hrs to 2030hrs. Total 1 no. of concrete truck, 1 no. of concrete pump and 2 nos. of vibratory pokers were in operation. According to RSS confirmed information, no construction works was conducted under Contract HY/2011/08 on 08 January 2018 from 1900hrs to 2300hrs at the concerned location. Meanwhile, concreting operation was conducted under Contract HY/2011/08 on 08 January 2018 from 1900hrs to 2300hrs at the concerned location. Meanwhile, concreting operation was conducted under Contract HY/2009/19 at Approach Ramp Phase 2 site area at Oil Street on 08 January 2018 from 1900hrs to 2300hrs. Total 1 no. of concrete pump and 2 nos. of vibratory pokers were operated without a valid Construction Noise Permit. In view of the above, the Contractor of HY/2009/19 was advised to i) fully review the Construction operations to ensure all construction operations during restricted hours strictly complies with the Construction Noise Permit and Noise Control Ordinance, ii) review the site control system for construction sequence and schedule to ensure all planned construction operations would be conducted within allowable period, shall any planned construction activities might extend beyond the specified allowed period, relevant necessary Construction Noise Permit(s) shall be applied for. In addition, the Contractor of HY/2009/19 is also recommended to provide briefing and training section to site staffs to enhance the site awareneess and understanding on r	Interim investigation report submitted to EPD on 23 January 2018. EPD advised no comment on 4 June 2018 on interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					noise permit(s) requirement during restricted hours. Follow up inspection during restricted hours was conducted by the Environmnetal Team on 18 January 2018, no construction operations was observed around the concerned location	
EPD complaint (H08/RS/000 01430-18) dated 17 January 2018	15 January 2018	An EPD complaint (Case Ref: H08/RS/0000143 0-18) referred to ET on 17 January 2018	2-8 Watson Road	Construction Dust was emitted from vehicles entering/ leaving construction site at 2-8 Watson Road	 An EPD complaint (Case ref: H08/RS/00001430-18) was referred to the ET on 17 January 2018. The complainant reported that construction dust was emitted from vehicles entering/leaving construction site at 2-8 Watson Road. ET confirmed with the Resident Site Staff that cable laying was conducted under Contract HY/2011/08 within the site area near Watson Road on 15 January 2018. No construction works was conducted under Contract HY/2009/19 near Watson Road on 15 January 2018. According to site information confirmed by RSS, cable laying was conducted under Contract HY/2011/08 within the site area near Watson Road on 15 January 2018. According to site information confirmed by RSS, cable laying was conducted under Contract HY/2011/08 within the site area near Watson Road on 15 January 2018 and no construction works was conducted under Contract HY/2009/19 near Watson Road on 15 January 2018. Based on review on relevant information, the concerned location of 2 – 8 Watson Road refers to a section of public road fronting the construction site entrance/ exit maintained by Contract HY/2009/19 at Watson Road. Follow up inspection was conducted by the Environmnetal Team on 17 January 2018. It was observed that wheel washing facilities and wheel washing for vehicles leaving from the construction site exit adjoining Watson Road was implemented by the Contractr HY/2009/19. No silt / soil deposition and no particular dust emission from the construction area under Contract HY/2009/19 and HY/2011/08 was observed. Seperately, it was observed that non-CWB project construction waste skip containing dusty demolition waste and rubbles was placed at the concerned section of public road at 2 – 8 Watson Road and it was further noticed that non-CWB projects had been undertaken around the concerned location. 	Interim investigation report submitted to EPD on 29 January 2018. EPD advised no comment on 4 June 2018 on interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Nevertheless, in view of the public concern, the Contractor of HY/2011/08 and the Contractor of HY/2009/19 were reminded to maintain the dust mitigation measures provided for the construction site and construction operation to avoid potential dust impact to the surroundings. The Contractor of HY/2009/19 was also reminded to upkeep the construction site exit control and wheel washing practice to maintain the proper condition of site entrance to avoid potential dust impact to the nearby public area.	
ICC complaint (CASE Ref: #2- 4459226093) dated 03 February 2018	3 February 2018	ICC complaint (CASE Ref: #2- 4459226093) dated 03 February 2018	Planter Area at Victoria Park boundary adjacent to footbridge to Victoria Park Road	Concern on an observed severely tilted tree with potential felling hazard. No fencing, no tree pit, trench and no irrigation pipe is observed	An ICC complaint referred by RSS was received by ET on 06 February 2018 (CASE#2-4459226093). The complainant reported that there is concern on an observed severely tilted tree with potential felling hazard. No fencing, no tree pit, trench and no irrigation pipe is observed. ET confirmed with Resident Site Staff that the concerned tree is within the works area of HY/2010/08 and one of the roots of the concerned tree (<i>Liquidambar formosana</i>) to have suffered minor damaged by the nearby excavation works. Remedial works including i) nylon reinforcement ropes has been added to the existing 3 nos. of tying cables and covering of the slope surface with wet hessian for protection were carried out for the damaged root of the tree. Follow up inspection was conducted by the Environmental Team on 09 February 2018. It was observed that the concerned tree has been fortified and protected for restoration and no tilting was observed. In view of the nearby construction works, the Contractor is suggested to demarcate the tree protection zone for the concerned tree and fence off the tree protection zone for the concerned tree and placing of construction material, if feasible. The Contractor is also suggested to provide refreshment training for frontline works for tree protection, in particular, for trees retained of site in close proximity to active works front to avoid potential damage to retained trees	Investigation Report issued on 26 February 2018 and case closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
EPD complaint (Case ref: H08/RS/0000 6600-18) was referred to the ET on 15 March 2018.	12 March 2018	An EPD complaint (Case ref: H08/RS/0000660 0-18) was referred to the ET on 15 March 2018.	Island Eastern Corridor near Wharf Road	Construction noise was emanated on Island Eastern Corridor (IEC) near Wharf Road at around 0800hrs on 12 March 2018	An EPD complaint (Case ref: H08/RS/00006600-18) was referred to the ET on 15 March 2018. The complainant reported that Construction noise was emanated on Island Eastern Corridor (IEC) near Wharf Road at around 0800hrs on 12 March 2018 ET confirmed with the Resident Site Staff that 1. No construction works was conducted under Contract HY/2009/19 on IEC near Wharf Road from 0730hrs to 0830hrs on 12 March 2018. According to RSS confirmed information, no construction works was conducted under Contract HY/2009/19 on IEC near Wharf Road from 0730hrs to 0830hrs on 12 March 2018 Nevertheless, in view of the public concern, the Contractor of HY/2009/19 was reminded to provide noise mitigation measure including temporary noise barrier and noise screen, as appropriate for potential noise impact associated works such as concrete breaking or cutting works, if any around the concerned location to avoid potential nuisance to surroundings.	The interim report would be submitted to EPD on 28 March 2018. EPD advised no comment on 4 June 2018 on interim report submitted and case closed.
EPD complaint was referred to the ET on 16 March 2018 and subsequent information clarified by EPD on 19 March 2018 (CASE Ref: H05/RS/0005 890-18).	4 March 2018	An EPD complaint was referred to the ET on 16 March 2018 and subsequent information clarified by EPD on 19 March 2018 (CASE Ref: H05/RS/0005890 -18).	Construction Site "China State" near Lung Wo Road and Fenwick Street	Noise and smoke was emanated from the idling motor of a loader/bulldozer at a construction site, "China State", near Lung Wo Road and Fenwick Pier at around 0700hrs at 04 March 2018.	 An EPD complaint was referred to the ET on 16 March 2018 and subsequent information clarified by EPD on 19 March 2018 (CASE Ref: H05/RS/0005890-18). The complainant reported that: Noise and smoke was emanated from the idling motor of a loader/bulldozer at a construction site, "China State", near Lung Wo Road and Fenwick Pier at around 0700hrs at 04 March 2018. ET confirmed with the Resident Site Staff that 1. No bulldozer/ loader was deployed on site under Contract No. HK/2012/08 around the concerned location on 04 March 2018 around 0700hrs. According to the RSS site information, No bulldozer/ loader was deployed on site under Contract No. HK/2012/08 around the concerned location on 04 March 2018 around 0700hrs. Follow up inspection was conducted by the Environmental Team, and no particular concern on dark smoke emission or noise emanation was observed from malfunctioning of the Powered Mechanical Equipment deployed on-site. Despite no 	The interim investigation report will be submitted to the EPD on 28 March 2018. EPD advised no comment on 7 May 2018 on interim report submitted and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					concerned equipment was deployed under Contract HK/2012/08 on site on the concerned date and location as confirmed with the RSS, in view of the public concern, the Contractor of HK/2012/08 is reminded to maintain regular checking and maintenance for powered mechanical equipment deployed on-site. Also the Contractor of HK/2012/08 is reminded to throttle down any idle equipment on-site to avoid potential nuisance to the surroundings.	
ICC complaint case referred to ET on 27 March 2018	12 March 2018	ICC complaint case referred to ET on 27 March 2018	Island Eastern Corridor Link	Construction noise emanation from Road Construction Works	An ICC complaint (Case Ref: 2-4495970766, lodged at 0955hrs on 12 March 2018) was referred to the ET on 27 March 2018. The ICC hotline operator reported that a public complaint was referred by the Police Force regarding noise emanation from road construction works at North Point section Island East Corridor (IEC) near 19 Wharf Road at around 0920hrs on 12 March 2018. Further information regarding the same event was received via ICC hotline (Case ref: 2-449606553, lodged at 1004hrs on 12 March 2018) was referred to the ET on 27 March 2018. The complainant further reported that noise was emanated from road construction works on Island Eastern Corridor (IEC) near Yu Lee Mo Fan Memorial School. Temporary noise barrier observed to be transparent in nature was speculated to be ineffective; and it was observed that only 3 out of the 6 units of temporary noise barrier are installed. The complainant suggested that additional 6 sections of noise barrier shall be installed. The noise emanation was started from 0800hrs and he is a resident at 18 Wharf Road and his rest was adversely affected by the concerned noise emanation. He has contacted the Environmental Protection Department and the Police Force regarding the noise emanation. The Environmental Protection Department has replied that construction works conducted after 0700hrs does not violate statutory requirement while the Police Force has created an ICC complaint case file (2-4495970766) for follow up.	Investigation Report issued on 12 April 2018 and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					head with acoustic material was implemented. Enhancement measures including provision of 2.5m high temporary noise barrier were subsequent implemented on 12 March 2018.	
					According to RSS confirmed information, concrete breaking works on IEC Eastbound near Pier F8 and Pier F9 was conducted under Contract HY/2009/19 from 0900hrs to 1000hrs on 12 March 2018. Noise mitigation measure including wrapping of breaking head with acoustic material was implemented. Enhancement measures including provision of 2.5m high temporary noise barrier were subsequent implemented on 12 March 2018.	
					Based on review on relevant site record, noise impact associated with the breaking works on IECL opposite to the concerned location was observed across March 2018 and project related exceedances were recorded at nearby noise monitoring station at YLMF Memorial School across March 2018. Upon identification of the project related exceedance at YLMF memorial school noise monitoring station, the Contractor is requested to adopt remedial and enhancement measures to minimize the noise emanation and avoid noise impact to the nearby sensitive receivers.	
					According to ET follow up checking, the following enahncement measures were proposed and implemented by the Contractor by 16 March 2018 :-	
					 Provide additional temporary noise barrier and repair damaged or incomplete temporary noise barrier installed for the breaking works Provide additional acoustics screen to the breaking tip in addition to temporary noise barrier installed Provide covering of breaker tip with acoustic material for noise reduction Conduct breaking works intermittently (No more than 15 mins within a 30 minutes interval) 	
					Nevertheless, subsequent to 16 March 2018 it was observed at times that the above mitigation measures were not fully implemented by the Contractor throughout the remaining breaking works period. Upon identification of	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					deficiency in mitigation measures, the Contractor has been requested to rectify any deficiency obserbed and ensure relevant noise mitigation measures are implemented and the observed deficiencies are rectified prior to resumption of the concerned impact associated works. According to Contractor information, the concerned breaking works have been completed by 26 March 2018.	
					In view of the public concern and the identified noise concern, the Contractor of HY/2009/19 was reminded that, shall future breaking works be required to be conducted on IECL (at works area located at the East of the noise enclosure), noise mitigation measure including but not limit to provision of temporary noise barrier with adequate height and extend and additional noise screen shall be proposed for ET/IEC review and confirmation prior to conducting the corresponding works to minimize the potential impact to the surroundings. The Contractor is also advised to review the adopt construction method with consideration on alterative PME with reduced noise emanation to minimize the potential noise impact to the surroundings.	
An ICC complaint (Case Ref: 2- 4530180777) was referred to the ET on 20 April 2018 An EPD complaint case (Case Ref: H08/RS/0000 9538-18) was referred to the ET on 23 April 2018	11 April 2018	An ICC complaint (Case Ref: 2- 4530180777) was referred to the ET on 20 April 2018 An EPD complaint case (Case Ref: H08/RS/0000953 8-18) was referred to the ET on 23 April 2018.	Island Eastern Corridor (Near Provident Centre, North Point)	Night time construction noise on Island Eastern Corridor outside Provident Centre at around 0110hrs on 11th April, 2018.	An ICC complaint (Case Ref: 2-4530180777) was referred to the ET on 20 April 2018. The complainant reported that Noise pollution was caused by the road works performed by some workers during midnight at Island Eastern Corridor (near Provident Centre, North Point) from time to time. They have used heavy noisy machinery and shouted quite often which disturbed the residents near Provident Centre in North Point seriously. An EPD complaint case (Case Ref: H08/RS/00009538- 18) was referred to the ET on 23 April 2018. According to EPD information, the complainant stated that Night time construction noise on Island Eastern Corridor outside Provident Centre at around 0110hrs on 11th April, 2018. As the location, time and concern of the above complaints cased received are identical, the two complaints will be reported and consolidated into one complaint case for reporting.	HyD will consolidate the input and reply to ICC and the interim investigation report was submitted to the EPD on 09 May 2018. EPD advised no comment on 4 June 2018 on interim report submitted and



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					ET confirmed with the Resident Site Staff that	case closed.
					1. No work was conducted under Contract HY/2009/19 from 2300hrs on 10 April 2018 to 0100hrs on 11 April 2018.	
					2. Installation and welding of steel frames of Traffic Sign FASS06 at works area opposite to Henrietta Secondary School was conducted under Contract HY/2009/19 between 0100hrs to 0600hrs on 11 April 2018.	
					3. Total 1no. of cherry picker, 1 no. of welding machine, 1 no. of lorry, 1 no. of grinder; 3 nos. of with flashing directional sign and 3 nos. of lorry mounted attenuator were deployed. Either one PME set consisting 1 no. of welding machine and 1 no. of cherry picker OR one PME set consisting of 1 no. of lorry and 1 no. of grinder were operated between 0100hrs to 0600hrs on 11 April 2018 at the concerned works area.	
					4. The following noise mitigation measures were implemented by Contractor of HY/2009/19 for the above construction works including:-	
					a) Operation of cherry picker within permanent noise barrier	
					b) Operation of welding machine and grinder inside acoustic enclosure	
					c) Switching off of lorry when idled	
					According to RSS confirmed information, no construction works was conducted under Contract HY/2009/19 from 2300hrs on 10 April 2018 to 0100hrs on 11 April 2018. Installation and welding of steel frames of Traffic Sign FASS06 at works area opposite to Henrietta Secondary School was conducted under Contract HY/2009/19 between 0100hrs to 0600hrs on 11 April 2018. Total 1 no. of cherry picker, 1 no. of welding machine, 1 no. of lorry, 1 no. of grinder; 3 nos. of with flashing directional sign and 3 nos. of lorry mounted attenuator were deployed. Either one PME set consisting 1 no. of welding machine and 1 no. of cherry picker OR one PME set consisting of 1 no. of lorry and 1 no. of grinder were	
					operated between 0100hrs to 0600hrs on 11 April 2018 at the concerned works area. Noise mitigation measures including i) Operation of cherry picker within permanent noise barrier and ii) Operation of welding machine and	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					grinder inside acoustic enclosure and iii) Switching off of lorry when idled were implemented by Contractor of HY/2009/19 for the above construction works. Relevant Construction Noise Permit numbered GW-RS0249-18 for the above construction works was in place for the construction works.	
					In view of the public concern on the shouting by the workers, the Contractor is also recommended to adopt "walkie-talkie" for communication to avoid potential nuisance caused to the nearby residents. The Contractor of HY/2009/19 was reminded to upkeep the site control system for construction works carried out during restricted hours and night time for Construction Noise Permit compliance and maintain regular maintenance of the plant and equipment deployed to avoid potential nuisance to the nearby public.	
180625	11 June 2018	An EPD complaint was referred to the ET on 25 June 2018 (CASE Ref: H05/RS/00015 954-18).	Construction Site near Wan Chai Pier	Construction dust and muddy water discharge was found at the site near Wan Chai Pier on 11 June 2018 afternoon.	ET confirmed with the Resident Site Staff that marine construction activity of removal of TWCR4 and stockpile of fill material at WCR3 Area were conducted under the Contractor of HK/2009/02 on 11 June 2018 afternoon. The Contractor of HK/2009/02 reported that double silt curtain was in place as mitigation measures during the marine activity and regular spraying water was provided as dust mitigation measures at WCR3 Area. Follow-up inspection was conducted on 28 June 2018, excavation works was observed at WCR3 Area and mitigation measures including watering during excavation was generally in place. Other dust mitigation measure includes covering the stockpile material and watering the dusty surface and haul road were generally in place. No particular dust impact was observed. No muddy water discharge or surface runoff related water quality monitoring impact was observed at Contract HK/2009/02 site area. Mitigation measures for marine activity includes providing double layers of silt curtain to enclose the marine activity area was generally in place and additional tarpaulin was provided to cover the temporary cut slope to avoid the potential	The interim report will be submitted to EPD on 4 July 2018. EPD advised no comment on 28 September 2018 on the interim investigation report and case closed.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					surface runoff. In view of the public concern, the Contractor of HK/2009/02 was reminded to keep review the performance of dust mitigation measures including watering during excavation and material handling, covering the stockpile material and watering the dusty surface and haul road to avoid potential dust impact and minimize any potential dust impact to the surroundings. The Contractor of HK/2009/02 was also reminded to maintain regular checking on the embankment, silt curtain and tarpaulin condition to ensure no gap / void to avoid potential water quality related impact.	
180831	31 August 2018	An EPD complaint was referred to the ET on 3 September 2018 (CASE Ref: H08/RS/00024 048-18).	Island Eastern Corridor outside Provident Centre	Night time construction noise on Island Eastern Corridor outside Provident Centre at around 1:00 a.m. on 31st August, 2018.	ET confirmed with the Resident Site Staff that 1) There was no construction activity undertaken by Contract HY/2011/08 at Island Eastern Corridor during the restricted hours from 2300hrs on 30 August 2018 to 0700hrs on 31 August 2018. 2) The Contractor of HY/2009/19 reported that paving work was conducted during the period of 0100hrs to 0600hrs at 31 August 2018 at the works area from D12 to F8 where was located inside the noise semi-enclosure of IEC. Total 4 nos. dump truck, 1 nos. paver, 1 no. vibratory roller and 1no. road roller with QPME label were used for the paving work. Relevant Construction Noise Permit GW-RS0679- 18 was in place for the construction works conducted during the above concerned periods. The PMEs operated during the concerned period was included in Construction Noise Permit GW-RS0679- 18 Condition 3.a. Group F. Based on RSS information, the noise control measure listed in Construction Noise Permit GW-RS0679- 18 Condition 3.d.9 including installation of engine exhaust silencers for asphalt paver and installation of absorbing lining to the engine compartment for road roller and vibratory roller were generally in place.	The interim report will be submitted to EPD on 14 September 2018.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Meanwhile, there is no sufficient information to conclude if the concerned asphalt paver installed with absorbing lining to the engine compartment; and concerned road roller and vibratory roller installed with engine exhaust silencers according to Construction Noise Permit GW-RS0679-18 Condition 3.d.9. In view of the above, the Contractor of HY/2009/19 was advised to critically check and confirm the noise control measures listed in Construction Noise Permit GW-RS0679-18 Condition 3.d.9 for concerned PMEs to ensure the operation of PMEs shall strictly follow the construction noise permit condition. The Contractor of HY/2009/19 was also reminded to maintain regular checking and maintenance of the PMEs and it's noise control measures deployed to avoid potential nuisance to the nearby public.	





Appendix 10.1

Construction Programme of Individual Contracts

ivity ID	Activity Name	Ori Dur	Rem Dur	Scheduled /Actual Start	Scheduled / Actual Finish	Total Float	Calendar	Augu 05 12	st 19	26	Septem	nber 16 23	2018
3 MONTHS F	ROLLING PROGRAMME OF WORKS PROGRAMME REVIEWED 8 AUG	2018 (DD 7-9-18)						00 12	13	20	02 09	10 23	30
EXCAVATION	N TWCR4 AND CONSTRUCTION OF WCR4											-	
EXCAVATE TV	VCR4 AND INSTALL SEAWALL												
A1000	TRANSPORT OF P5 FILL MATERIAL TO P34	10	10	30-Oct-18	08-Nov-18	32	HK Working Day						
MARINE EXC	AVATION							1	1				
A1030	WEST SIDE EXC FOR G400 (1600M3) & 0.5TARMOUR	20	20	07-Sep-18*	26-Sep-18	0	7-Day Workweek-1						WEST SIDE EX
A1040	ARRIVAL OF G400	1	1	17-Sep-18	17-Sep-18	143	7-Day Workweek-1				-	ARRIVALO	F G400
A1050	ARRIVAL OF ARMOUR	1	1	21-Sep-18	22-Sep-18	134	HK Working Day					L <mark>≻∎</mark> ARR	NAL OF ARMOL
CUTTING D-V	VALL							1	-				
A1080	EAST SIDE CORE HOLES	9	1	01-Sep-18 A	07-Sep-18	16	7-Day Workweek-1	1			EAST SIDE	E CORE HOLE	S
A1090	WEST SIDE CORE HOLES	5	5	05-Sep-18 A	12-Sep-18	16	7-Day Workweek-1			4	WES	ST SIDE CORE	HOLES
A1100	VERTICAL CUT	20	5	05-Sep-18 A	11-Sep-18	13	7-Day Workweek-1	1	-	-•	VER	TICAL CUT	
A1110	HORIZONTAL CUT	20	20	07-Sep-18	26-Sep-18	5	7-Day Workweek-1	1	-		-		HORIZONTAL C
A1120	REMOVAL OF D-WALL	20	20	07-Sep-18	26-Sep-18	5	7-Day Workweek-1	-	: : :			<u> </u>	REMOVAL OF I
INSTALL SEA	WALL							1					
MANUFACTUR	RE OF SEAWALL BLOCK												
A1125	MANUFACTURE OF SEAWALL BLOCK	86	43	27-Jul-18 A	19-Oct-18	40	7-Day Workweek-1					· · · · · · · · · · · · · · · · · · ·	
A1127	MANUFACTURE OF FACING STONE	15	15	20-Oct-18	03-Nov-18	103	7-Day Workweek-1						
A1130	1ST DELIVERY	1	1	13-Sep-18*	13-Sep-18	19	7-Day Workweek-1	1	-		[1S	TDELIVERY	
A1140	2ND DELIVERY	1	1	06-Oct-18*	06-Oct-18	9	7-Day Workweek-1	1					►1 21
A1150	3RD DELIVERY	1	1	12-Oct-18*	12-Oct-18	17	7-Day Workweek-1						
A1160	4TH DELNERY	1	1	19-Oct-18*	19-Oct-18	11	7-Day Workweek-1	1					
A1170	5TH DELNERY	1	1	27-Oct-18*	27-Oct-18	4	7-Day Workweek-1		1				
A1180	6TH DELNERY	1	1	02-Nov-18*	02-Nov-18	3	7-Day Workweek-1	1	-				
A1190	7TH DELNERY	1	1	09-Nov-18*	09-Nov-18	6	7-Day Workweek-1	-		· · · · · · · · · · · · · · · · · · ·			
A1200	8TH DELNERY	1	1	15-Nov-18*	15-Nov-18	14	7-Day Workweek-1						
INSTALLATIO	N OF EAST SIDE SEAWALL BLOCK				-				-				
A1210	MOUNTING ROCK BEDDING	6	6	19-Sep-18	24-Sep-18	19	7-Day Workweek-1	1				M	OUNTING ROCH
A1220	LEVELLING	3	3	25-Sep-18	27-Sep-18	19	7-Day Workweek-1	1	-				LEVELLING
A1230	M9 BLOCK	2	2	28-Sep-18	29-Sep-18	19	7-Day Workweek-1					4	- M9 BLOCK
A1240	LEVELLING	5	5	30-Sep-18	04-Oct-18	19	7-Day Workweek-1						LEVI
A1250	1ST LAYER OF BLOCK	4	4	05-Oct-18	08-Oct-18	19	7-Day Workweek-1	1	-				
A1260	2ND LAYER	3	3	09-Oct-18	11-Oct-18	19	7-Day Workweek-1						-
A1270	3RD LAYER	3	3	12-Oct-18	14-Oct-18	19	7-Day Workweek-1	1					
A1280	4TH LAYER	3	3	15-Oct-18	17-Oct-18	19	7-Day Workweek-1		-				
A1290	5TH LAYER	3	3	18-Oct-18	20-Oct-18	19	7-Day Workweek-1			[
A1300	6TH LAYER	3	3	21-Oct-18	23-Oct-18	19	7-Day Workweek-1	-					
A1310	TYPEA	4	4	24-Oct-18	27-Oct-18	19	7-Day Workweek-1	1	-				
A1320	GEOTEXTILE AND FILTER	4	4	28-Oct-18	31-Oct-18	19	7-Day Workweek-1	1					
A1330	B/F SOIL (5000m3)	8	8	01-Nov-18	08-Nov-18	19	7-Day Workweek-1	1					
A1340	PLACE CONC CUBES AND PARTLY B/F TO +3.5mPD (1000m3)	6	6	09-Nov-18	14-Nov-18	19	7-Day Workweek-1						
INSTALLATIO	N OF WEST SIDE SEAWALL BLOCK							8	8				
A1370	MOUNTING ROCK BEDDING TYPE 12A & 12B	15	15	27-Sep-18	11-Oct-18	0	7-Day Workweek-1	1	-			اها ا	
A1380	LEVELLING	4	4	12-Oct-18	15-Oct-18	0	7-Day Workweek-1	1					
A1390	M9 BLOCK	3	3	16-Oct-18	18-Oct-18	0	7-Day Workweek-1						
A1400	LEVELLING	7	7	19-Oct-18	25-Oct-18	0	7-Day Workweek-1						
A1410	1ST LAYER OF BLOCK	6	6	26-Oct-18	31-Oct-18	0	7-Day Workweek-1	1					
A1420	2ND LAYER	5	5	01-Nov-18	05-Nov-18	0	7-Day Workweek-1	1				-	
A1430	3RD LAYER	5	5	06-Nov-18	10-Nov-18	0	7-Day Workweek-1	-		· · · · · · · · · · · · · · · · · · ·			
A1440	4TH LAYER	5	5	11-Nov-18	15-Nov-18	0	7-Day Workweek-1						
A1450	5TH LAYER	4	4	16-Nov-18	19-Nov-18	0	7-Day Workweek-1						
A1460	6TH LAYER	3	3	20-Nov-18	22-Nov-18	0	7-Day Workweek-1	1					
A1470	TYPEA	4	4	23-Nov-18	26-Nov-18	0	7-Day Workweek-1		-				
A1480	FILTER	4	4	27-Nov-18	30-Nov-18	0	7-Day Workweek-1	1					
						-			i.				
A1490	B/F TO +2.8m PD	6	6	01-Dec-18	06-Dec-18	0	7-Day Workweek-1	1			1 E E		

•	◆ IVIIIestone			Date	
•	 Critical Milestones 	CHUN WO - CRGL	CEDD CONTRACT NO. HK/2009/02		
	Current Works	JOINT VENTURE	WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)		
	Critical Works		3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)		-
_	Remaining Level of				┢
	i torrion ng Eovor onni				

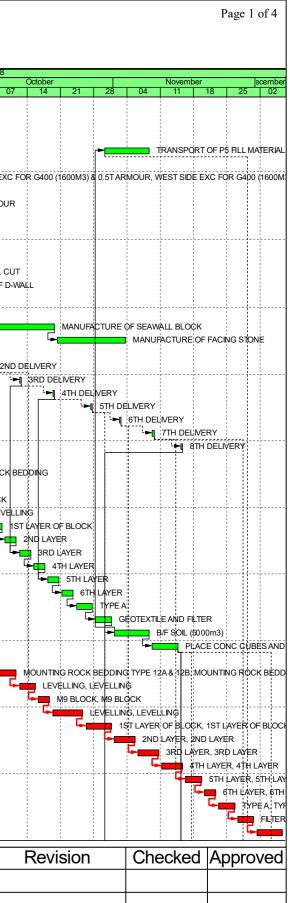




REINSTATE BAY 1 A1540 HELIPAD A1600 A1610 A1620 A1630 A1640 A1650 A1660 A1650 M1670 COPING WITHIN D-WALL (T A1780	2 SEAWALL 2 SEAWALL NSTALL SEAWALL DISMANTLE OLD SEAWALL BLOCK AND EXCAVATE ROCKFILL G400 LEVELLING 1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 5TH LAYER 5TH LAYER		4	30 14 3	30-Nov-18 01-Nov-18	30-Dec-18	15	7-Day Workweek-1	05	12 1	26	02	09	16	23 3	30
A1540 HELIPAD A1600 A1610 A1620 A1630 A1630 A1650 A1660 A1660 A1670 COPING WITHIN D-WALL (T	NSTALL SEAWALL DISMANTLE OLD SEAWALL BLOCK AND EXCAVATE ROCKFILL G400 LEVELLING 1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER		4	14		30-Dec-18	15	7-Day Workweek-1		-	8				-	
HELIPAD A1600 A1610 A1620 A1630 A1650 A1660 A1670 COPING WITHIN D-WALL (1)	DISMANTLE OLD SEAWALL BLOCK AND EXCAVATE ROCKFILL G400 LEVELLING 1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER		4	14		30-Dec-10	15	I-Day WORWEER-I								
A1600 A1610 A1620 A1630 A1640 A1650 A1660 A1660 A1670 COPING WITHIN D-WALL (T	ROCKFILL G400 LEVELLING 1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER	: : : : : : : : : : : : : : : : : : : :	3		01 Nev 19				-		1					-
A1610 A1620 A1630 A1640 A1650 A1660 A1670 COPING WITHIN D-WALL (T	ROCKFILL G400 LEVELLING 1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER	: : : : : : : : : : : : : : : : : : : :	3			14-Nov-18	14	7-Day Workweek-1			1				1	
A1620 A1630 A1640 A1650 A1660 A1670 COPING WITHIN D-WALL (T	LEVELLING 1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER				15-Nov-18	17-Nov-18	14	7-Day Workweek-1 7-Day Workweek-1		-	1				-	
A1630 A1640 A1650 A1660 A1670 COPING WITHIN D-WALL (T	1ST LAYER OF SEAWALL BLOCK 2ND LAYER 3RD LAYER 4TH LAYER		·	3	18-Nov-18	20-Nov-18	14	7-Day Workweek-1								
A1640 A1650 A1660 A1670 COPING WITHIN D-WALL (T	2ND LAYER 3RD LAYER 4TH LAYER	:	2	3	21-Nov-18	23-Nov-18	14	7-Day Workweek-1			1				-	
A1650 A1660 A1670 COPING WITHIN D-WALL (T	3RD LAYER 4TH LAYER			3	24-Nov-18	26-Nov-18	14	7-Day Workweek-1		-						
A1660 A1670 COPING WITHIN D-WALL (T	4TH LAYER		4	4	27-Nov-18	30-Nov-18	14	7-Day Workweek-1					1			
A1670 COPING WITHIN D-WALL (T				3	01-Dec-18	03-Dec-18	14	7-Day Workweek-1			1				1	
COPING WITHIN D-WALL (T			3	3	01-Dec-18	06-Dec-18	14									
WITHIN D-WALL (T	SITERER		J	J	04-Dec-10	00-Dec-10	14	7-Day Workweek-1			1				-	
										-						
A1780				44	07.0 40*	00.0 40	50	7 Day Wedays als 4								
	BAY 1 LOWER			14	07-Sep-18*	20-Sep-18	56	7-Day Workweek-1			1		-		1 LOWER	
A1790	BAY 2 LOWER			13	21-Sep-18	03-Oct-18	56	7-Day Workweek-1						····		BAY
A1800	BAY 1 UPPER		7	7	04-Oct-18	10-Oct-18	56	7-Day Workweek-1			1					1
A1810	BAY 2 UPPER		7	7	11-Oct-18	17-Oct-18	56	7-Day Workweek-1		-						
EAST SIDE COPIN										-						
A1830	EAST COPING	3	1	31	17-Nov-18	17-Dec-18	39	7-Day Workweek-1								i i
BOX-O																
ARRIVAL OF PRE	CAST UNIT FOR BAY 12														ļ	
A1840	ARRNAL OF PRECAST UNIT FOR BAY 12		1	1	07-Sep-18*	07-Sep-18	62	7-Day Workweek-1		-			ARRIVAL	OF PRECA	ST UNIT FC)R BÁY
INSTALLATION O	F PRECAST UNIT															
A1850	INSTALLATION OF PRECAST UNITS	1	9	19	25-Oct-18	13-Nov-18	15	7-Day Workweek-1		-	1				1	
A1860	BAY 1 FIX REBAR		2	2	01-Nov-18	03-Nov-18	15	7-Day Workweek-1								
A1870	BAY 1 CONCRETE			1	03-Nov-18	04-Nov-18	15	7-Day Workweek-1								
A1880	BAY 2 FIX REBAR		2	2	06-Nov-18	08-Nov-18	15	7-Day Workweek-1								
A1890	BAY 2 CONCRETE			1	08-Nov-18	09-Nov-18	15	7-Day Workweek-1								
A1900	BAY 3 FIX REBAR			2	13-Nov-18	15-Nov-18	15	7-Day Workweek-1		-					1	
A1910	BAY 3 CONCRETE			1	15-Nov-18	16-Nov-18	15	7-Day Workweek-1								
A1920	CLEAN UP, W/P AND B/F			13	17-Nov-18	30-Nov-18	15	7-Day Workweek-1				·				
CONSTRUCTION		1	5	13	17-1100-10	30-1104-10	15	T-Day WORWEEK-T								
										1						
REMOVAL OF BUI		i -		0	01.0 10.1	05.0 40.4										
A1930	BAY 19 STEEL BULKHEAD			0	01-Sep-18 A	05-Sep-18 A		7-Day Workweek-1						EL BULKHE		
A1940	BAY 13 CONCRETE BULKHEAD		5	1	04-Sep-18 A	08-Sep-18	15	7-Day Workweek-1	·			· · · · · · · · · · · · · · · · · · ·		CONCRETE		
A1950	CONSTRUCTION OF EARTH PLATFORM		6	6	08-Sep-18	14-Sep-18	15	7-Day Workweek-1		-				CONSTRUC	, TION OF E	ARTH
PIPE PILING AND																
A1960	WEST SIDE PIPE PILING		0	3	01-Aug-18 A	09-Sep-18	17	7-Day Workweek-1				i I	WEST	SIDE PIPE F		
A1970	WEST SIDE GROUTING			15	21-Aug-18 A	22-Sep-18	146	7-Day Workweek-1			:	:		V	VEST SIDE	:
A1980	EAST SIDE PIPE PILING			13	11-Sep-18	24-Sep-18	15	7-Day Workweek-1					4 >		EAST SID	
A1990	EAST SIDE GROUTING	1	1	11	20-Sep-18	01-Oct-18	15	7-Day Workweek-1							، <mark>ہے</mark>	EAST
EXCAVATION AND																
A2000	DEMOLISH OLD CULVERT, CUT STEEL PILE AND INSTALL ELS	1	0	10	21-Sep-18	01-Oct-18	15	7-Day Workweek-1							· 🚍 💻	DEMO
A2010	EXCAVATE TP -2.9mPD	8	3	8	01-Oct-18	09-Oct-18	15	7-Day Workweek-1							₩	;_
A2020	B/F G200 & ELS	8	8	8	09-Oct-18	17-Oct-18	15	7-Day Workweek-1								
A2030	TAMPING	2	2	2	17-Oct-18	19-Oct-18	15	7-Day Workweek-1								
A2040	LEVELLING	:	5	5	19-Oct-18	24-Oct-18	15	7-Day Workweek-1								
HUNG HING ROA	AD									-						
REMOVAL OF D-	VALL TO +1.5mPD															i i
A2050	ZONEA	2	1	0	13-Jul-18 A	25-Aug-18 A		7-Day Workweek-1	1	:	ZONEA					
A2060	ZONE B		6	5	01-Sep-18 A	11-Sep-18	110	7-Day Workweek-1		- [70	NE B		·
A2070	ZONE C		4	14	17-Nov-18	30-Nov-18	44	7-Day Workweek-1								
	ZONE C	1	4	14	17-1100-10	30-1100-18	44	7-Day WOIKWEEK-1								
BACKFILLING			-								<u> </u>				-	
A2090	ZONEA		5	0	17-Aug-18 A	30-Aug-18 A		7-Day Workweek-1		· •	Z	ÓNE A			_	
A2100	ZONE B		7	7	11-Sep-18	18-Sep-18	149	7-Day Workweek-1					₩	ZONE	В	
▲ N 4:1	tana														Date	<u>.</u>
 Miles 	lone													F	Duit	<u> </u>
	al Milestones CHUN WO - CRGL				CEDD		лот	[.] NO. HK/2	2000	///2						
	al Milestones CHUN WO - CRGL								-003	n VZ				F		+
	ent Works JOINT VENTURE	_ וו סעע	<u>]</u> er	ntra	al Wanc	hai Rvi	าลรร	at Wan C	hai	Fast	(Con	trac	t 2)			


3-MONTH ROLLING PROGRAMME (data date 07-Sep-18)

Remaining Level of...

Critical Works

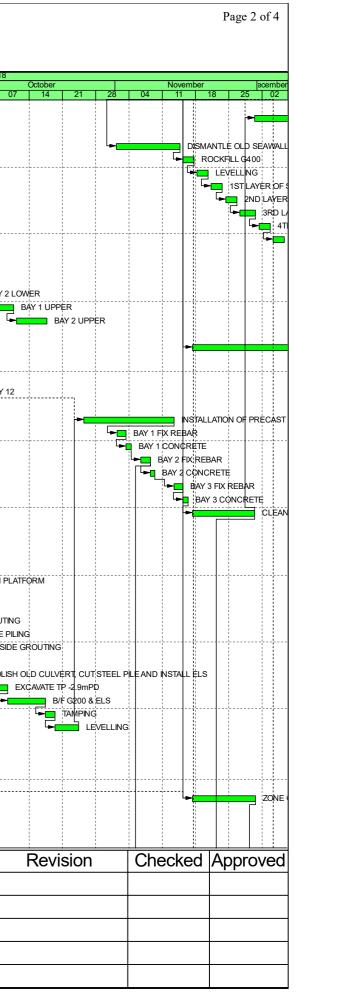

tivity ID	Activity Name		Ori Dur	Rem Dur	Scheduled /Actual Start	Scheduled / Actual Finish	Total Float	Calendar	Augu		20		September	00		18
A2110	ZONE C		5	5	01-Dec-18	05-Dec-18	71	7-Day Workweek-1	05 12	19	26	02 0	09 16	23	30	07
MANHOLE			Ŭ	Ū	01 200 10	00 200 10		1 Day Holkitock 1								
A2130	MH7352A		8	6	05-Sep-18 A	12-Sep-18	106	7-Day Workweek-1					MH7352A			
A2140	MH7354&7355		10	7	05-Sep-18 A	19-Sep-18	106	7-Day Workweek-1		-				MH7354&73	55	
A2150	MH7341		9	9	19-Sep-18	28-Sep-18	106	7-Day Workweek-1							MH7341	
DRAOMAGE								,								
CH3730-3760																
A2200	375MM DRAIN FROM SMH7354	TO BOX	16	0	31-Jul-18 A	18-Aug-18 A	1	7-Day Workweek-1		375MM	DRAIN FR	ом <mark>s</mark> мн738	54 TO BOX			
A2210	375M SMH7355 TO 7354		13	4	20-Aug-18 A	10-Sep-18	16	7-Day Workweek-1		(<u>-</u>			375M \$MH7	355 TO 735	4	
A2220	300MM SMH734F1 TO 7355		11	10	03-Sep-18 A	21-Sep-18	16	7-Day Workweek-1					; i	300MM S	MH734F	TO
A2230	BACKFILLING		13	13	21-Sep-18	04-Oct-18	16	7-Day Workweek-1			L			l	В	ACKF
A2240	AIR TEST AND CCTV		3	3	04-Oct-18	07-Oct-18	16	7-Day Workweek-1							┕►	AIF
BCO													8			
A2250	600MM DRAIN SMH7352A TO BC	XC	11	0	30-Jul-18 A	09-Aug-18 A		7-Day Workweek-1	600MM D	RAIN SMH	7352A TO E	BOX				
A2260	BAY 12 (1200MM TO BOX)		8	8	07-Nov-18	15-Nov-18	22	7-Day Workweek-1								
A2270	BAY 12 TO 14 GULLIES AND 225	DRAIN	12	12	24-Nov-18	06-Dec-18	22	7-Day Workweek-1			L					
CH3730-3760 RE	MAINING				,								1 1 1			
A2280	300MM DRAIN SMH7341 TO 735	3	9	9	06-Dec-18	15-Dec-18	22	7-Day Workweek-1		-			1			
ROADWORK													1			
HHR													1 1 1			
A2390	ROAD FORMATION		12	12	30-Sep-18	12-Oct-18	16	7-Day Workweek-1							-	
A2400	TESTING		10	10	12-Oct-18	22-Oct-18	16	7-Day Workweek-1					5 5 5			G
A2410	KERB		8	8	22-Oct-18	30-Oct-18	16	7-Day Workweek-1		-			1			
A2420	SUB-BASE		12	12	30-Oct-18	11-Nov-18	16	7-Day Workweek-1								
A2430	TEST		8	8	11-Nov-18	19-Nov-18	16	7-Day Workweek-1					1			
A2440	ROAD FORMATION		3	3	19-Nov-18	22-Nov-18	16	7-Day Workweek-1								
A2450	TEST AND SUB-BASE		11	11	22-Nov-18	03-Dec-18	16	7-Day Workweek-1					1			
A2460	ROAD FURNITURE		14	14	28-Nov-18	12-Dec-18	16	7-Day Workweek-1					1			
A2470	BLACK TOP		9	9	03-Dec-18	12-Dec-18	16	7-Day Workweek-1		-			1			
600mm Sewere	9												1			
FIRST STAGE																
A2500	600MM SEWER		5	1	26-Jul-18 A	07-Sep-18	97	7-Day Workweek-1		:		600	MM SEWER			
A2510	B/F		5	5	08-Sep-18	12-Sep-18	97	7-Day Workweek-1					B/F			
A2520	SUB-BASE		9	9	13-Sep-18	21-Sep-18	97	7-Day Workweek-1				Ģ	· · ·	SUB-BAS	E	
A2530	BLACKTOP		2	2	22-Sep-18	23-Sep-18	97	7-Day Workweek-1		ł			Ģ	BLACK	KTOP	
A2540	TTA		1	1	24-Sep-18	24-Sep-18	97	7-Day Workweek-1		-				🛏 ПА		
SECOND STAGE					· ·					-			1	ſ		
A2550	600MM SEWER		12	12	25-Sep-18	06-Oct-18	97	7-Day Workweek-1		-						600
A2560	B/F		5	5	07-Oct-18	11-Oct-18	97	7-Day Workweek-1							L.	
A2570	SUB-BASE		9	9	12-Oct-18	20-Oct-18	97	7-Day Workweek-1					5 5 5			Ģ
A2580	BLACKTOP		2	2	21-Oct-18	22-Oct-18	97	7-Day Workweek-1			L		·			
A2590	TTA		1	1	23-Oct-18	23-Oct-18	97	7-Day Workweek-1								
FINAL STAGE													1			
A2600	600MM SEWER mh4.13 TO 4.15	TO 4 17	11	11	24-Oct-18	03-Nov-18	97	7-Day Workweek-1								
A2610	AIR TEST		1	1	04-Nov-18	04-Nov-18	97	7-Day Workweek-1					- 			
A2620	b/f		3	3	05-Nov-18	07-Nov-18	97	7-Day Workweek-1								
A2630	AIR TEST AND CCTV		2	2	08-Nov-18	09-Nov-18	97	7-Day Workweek-1								
	VCR1 & WCR3 REMAINING	NODKS	_	-	00110110	00110110	01	1 Buy Hondrook 1					1			
		MORKS			00 1-140 4	00.0 40	404	7 Day Wadaya ala 4								
A2650			11	1	28-Jul-18 A	08-Sep-18	101	7-Day Workweek-1		:			/IS INSTALLA			
A2660	WCR1 U CHANNELS		50	50	07-Sep-18*	26-Oct-18	52	7-Day Workweek-1								
A2670	EXPO DRIVE COVER REMEDIAL	-	46	23	15-Aug-18 A	29-Sep-18	123	7-Day Workweek-1		:	1		i.		EXPO D	RIVE
A2680	EXPO DRIVE COPING		28	28	17-Sep-18	14-Oct-18	123	7-Day Workweek-1		-						_
A2690	WCR1 EVA		59	59	01-Nov-18*	29-Dec-18	47	7-Day Workweek-1					1			
A2700	WCR3 SUB-BASE		24	24	17-Nov-18*	10-Dec-18	61	7-Day Workweek-1					1			
A2710	REPAIR COPING		11	11	29-Nov-18*	09-Dec-18	67	7-Day Workweek-1								
	- 4													Da	ate	
Mile:	sione															
	ool Milesterse	CHUN WO - CRGL			CEDD	CONTE	20CT	⁻ NO. HK/2	nna/n	2						
Critic	cal Milestones				CLDD	CONTR		NO. 1177	.003/0	2						
	$a = 1 \wedge 1 = 1 + 2$	JOINT VENTURE	WD II - Ce	entr	al Wand	hai By	nass	at Wan C	hai Fa	nst ((Contr	act 2	4			
	ent Works									-			7			
				TUT				ヽヽヽヽヽロ (えっ・	to date	<u> 07 </u>	Con	10\				
	ool Works				RULLIN		UGRA		la uale	; 0/-	Sep-	101				
Critic	cal Works		3-10101		RULLIN		GRA	AMME (da	la uali	= 07-	Seh-	10)				
	cal Works naining Level of		3-141014		RULLIN		GRA	AIVIIVIE (Ua	la uale	= 07-	Seh-	10)				

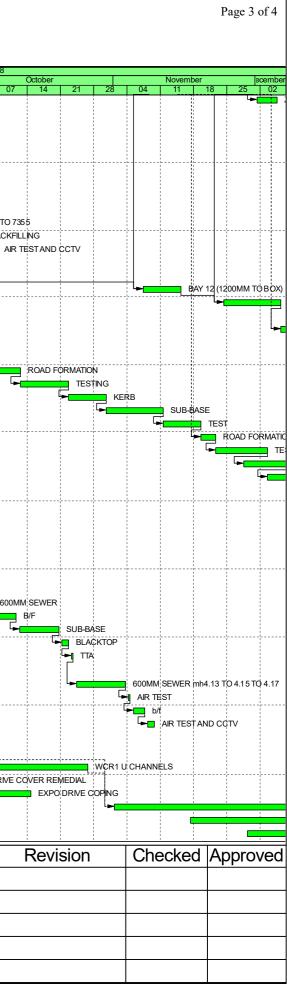

Activity ID	Activity Name	Ori	Rem	Scheduled	Scheduled /	Total	Calendar		August				Sonta	ombor		20	018	October				Novem	bor		combor
		Dur	Dur	/Actual Start	Actual Finish	Float		05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02
A2720	WCR1&3 ARMOUR SLOPE PROFILE	31	31	01-Dec-18*	31-Dec-18	45	7-Day Workweek-1							1										ſ	
A2740	REINSTATE WCR3 EXIT	23	23	24-Sep-18*	16-Oct-18	121	7-Day Workweek-1							1			:	RI	EINSTATE	WCR3 E	хп				
A2750	WCR3 FENCING	23	23	09-Nov-18*	01-Dec-18	75	7-Day Workweek-1			-		1 1 1	1	1 1 1		1 1 1	1		-			1	1	-	WCR

 Milestone Critical Milestones Current Works Critical Works Remaining Level of CHUN WO - CRGL JOINT VENTURE CEDD CONTRACT NO. HK/2 WD II - Central Wanchai Bypass at Wan Ch 3-MONTH ROLLING PROGRAMME (data 	nai East (Contract 2)	Revision	Checked A	Approved
---	-----------------------	----------	-----------	----------

Page 4 of 4

	Activity Name	Rem Dur	Start	Finish	Augus	t		Sent	ember		20
		Dui			12	19	26	02 09	16	23	30 0
IRP (Aug 2	2018 - Nov 2018)										
- SECTION	2 & 2A OF THE WORKS										
5.3 - Box Cu	lvert T1										
	statement Works Around Box Culvert T1	,									
0620-2150	Install new concrete blocks (19 Nos)	6	03-Aug-18 A	25-Aug-18			Install n	ew concrete	e blocks	s (19 Nos	s)
0620-2170	Backfill with Rockfill Type A (156 m3)	3	27-Aug-18	29-Aug-18			► Bao	kfill with Ro	ckfill Ty	pe A (156	6¦m3)
0620-2180	Geotextile and granular fill (135 m3)	2	30-Aug-18	31-Aug-18				eotextile an	ıd granı	ılar fill (13	35 m3)
0620-2190	General fill to required level (320 m3)	2	01-Sep-18	03-Sep-18				General fi	ll to requ	uired leve	el (320 m3)
0620-2200	Construct Mass Concrete Copping (110 m3)	15	04-Sep-18	20-Sep-18			L	•		Constru	uct Mass Co
- SECTION	I 3 OF THE WORKS										
6.3 - Admin E	Building										
Admin Buildir	ng - Outstanding Works After Hanover to CC										
0630-2767	Drainage Downpipe near Abutment D12 (expecting Handover back from CC by 1 August 2018)	12	27-Aug-18*	08-Sep-18				Drai	nage Do	ownpipe	near Abutm
0630-2769	Abutment D12 Masking Wall	12	30-Aug-18	12-Sep-18	_				Abutme	nt D12 N	/lasking Wa
0630-2771	Removal of Temporary Noise Barrier	4	11-Sep-18	14-Sep-18					Remo	oval of Te	emporary No
0630-2777	Run-in at ADB carpark entrance & SR 13 (expecting Handover back from CC by 1 August) 2018	15	27-Aug-18*	12-Sep-18					Run-in a	at ADB c	arpark entr
0630-2781	Oil Street Cul-de-sac Reinstatement (expecting Handover back from CC 1-August-2018)	15	27-Aug-18*	12-Sep-18					Oil Stree	et Cul-de	-sac Reins
0630-2787	Traffic Signage at OI Street Cul-de-sac	9	18-Aug-18 A	05-Sep-18	╡└╾┓			Traffic S	Signage	at Oil Str	reet Cul-de-
) - SECTION	X OF THE WORKS										
	Bridge (Bridge F)										
	e Construction										
Bridge F1B2 1032-3921.3		1	25-Aug-18*	25-Aug-18			Bridge I	=1B2 - East	Bound	- Surfaci	ing (2nd Lay
1032-3921.4	Bridge F1B2 - East Bound - Surfacing (3rd Layer)	1	09-Sep-18*	09-Sep-18			· · · ·	 Bric	lge F1E	32 - East	Bound - Su
1032-3925	Bridge F1B2 - East Bound - Marking	5	10-Sep-18	14-Sep-18					•		East Bound
							·				
Bridge F1B1 1032-1822.3	Bridge F1B1 - West Bound - Surfacing (3rd Layer)	1	25-Aug-18*	25-Aug-18			Bridge	=1B ⁻ - Wes	t Bound	I - Surfac	cing (3rd La
1032-1822.4	Bridge F1B1 - West Bound - Surfacing (4th Layer)	1	08-Sep-18*	08-Sep-18				Bride	ge F1B1	I - West	Bound - Su
	Bridge F1B1 - West Bound - Marking	5	10-Sep-18	14-Sep-18	-			L.	-		West Bour
1032-1824								•			
	idae F (Common)		16-Jun-18 A	10-Sep-18		 	·	(G	ireen Ro	oof @ F2	2): - Down P
	ridge F (Common) (Green Roof @ F2) - Down Pipe, Drainage system & Gutter	19									· · · · · · · · · · · · · · · · · · ·
All Middle Br	(Green Roof @ F2) - Down Pipe, Drainage system & Gutter	19 10	01-Aug-18 A	30-Aug-18			(0	ireen Roof (@ F3 - E	Excl abov	ve live trafic
All Middle Br 1032-4359.3	(Green Roof @ F2) - Down Pipe, Drainage system & Gutter (Green Roof @ F3 - Excl above live trafic) - Screeding			30-Aug-18 12-Sep-18			(G				i i
All Middle Br 1032-4359.3 1032-4360.2	 (Green Roof @ F2) - Down Pipe, Drainage system & Gutter (Green Roof @ F3 - Excl above live trafic) - Screeding (Green Roof @ F3 - Down Pipe, Drainage system & Gutter 	10	01-Aug-18 A								ve live trafic F3 - Down

Effort			Critical Remaining Work
	•	•	Milestone

Actual Work

Contract HY/2009/19 Three Months Rolling Programme (20.Aug.2018 to 20.Nov.2018)

	01	0	04	Novem			ember
14	21	28	04	11	18	25	02
						1	
						1	
						1	
						1	
						 , ,	
						1	
						1	
						1	
rete Cop	noina (1	10 m3)				1	
	-pg (i						
		 				י י י	
		1					
_					_		
: D12 (e>	pecting	y Hando	overba	ck from	CC by	1 Augu	ust 201
						1	
						1	
e Barrier						1	
	0 ((
e & SR1	13 (expe	ecting F	landov	er back	from CO	бут	Augus
ement (e	vnectin	a Hand	over ha	ack from	n CC 1-4		-2018)
	xpcouri	griana			10017	lugust	2010)
с							
G						1	
						1	
)							
cing (3rd	d Layer)					1	
Marking						1	
		 				י י א	
)							
cing (4th	Layer)					1	
Marking						1	
iviai kii ig)						
		 				, , ,	
, Drainag	ge syste	em & Gi	utter				
Screedir	ng					1	
e, Draina		tem & C	Auttor				
o, Dialità	ige sys						
_						1	
t, Frame	& Sign	face					
			1			1	
				P	age 1 of 4	4	

ty ID	Activity Name	Rem	Start	Finish	2018
		Dur			August September 12 19 26 02 09 16 23 30 07
1032-4387.02	WB-Traffic Sign RS08 at F15 JTI (NW) Bolt, Frame & Sign face	6	07-Sep-18	12-Sep-18	W <mark>8</mark> -Traffic Sign RS08 at F15
1032-4387.03	WB-Modification ofTemp Sign near P32 (NW)	3	04-Sep-18	06-Sep-18	→ WB-Mod fication of Temp Sign near F
1032-4387.04	WB-Modification of exist Sign DS07 (NW)	5	30-Aug-18*	03-Sep-18	WB-Modification of exist Sign DS07 (N
1032-4387.05	WB-Road Sign Post TSP46 & 50-Drilling, Holding Down Bolt & Post	6	30-Aug-18*	04-Sep-18	WB-Road Sign Post TSP46 & 50-Drilli
1032-4387.06	WB-Road Sign Post TSP43 & 44-Drilling, Holding Down Bolt & Post	6	01-Sep-18	06-Sep-18	WB-Road Sign Post TSP43 & 44-Dr
1032-4387.07		5	04-Sep-18	08-Sep-18	₩B-Road Sign Post TSP35-Drillin
1032-4387.08		6	05-Sep-18	10-Sep-18	EB-Road Sign Post TSP47 & 48
1032-4387.09		5	09-Sep-18	13-Sep-18	EB-Road Sign Ppst TSP56(1
		J	09-0ep-10	10-0ep-10	
Outstanding V					
1032-4400	Corbel Const & Replacement of Temporary Lighting to Permanent at F4-F5 (NW)	28	15-Sep-18	20-Oct-18	
1032-4420	Replacement of Temporary L3 Railing to Permanent Between Pier F8-F14 (NW)	28	02-Oct-18	03-Nov-18	
1032-4430	Install remaining standard traffic & directional sign (NW)	28	02-Oct-18	03-Nov-18	
1032-4440	Removal of Temporary JTI sign gantry at Tong Sui Slip Road (NW)	28	05-Nov-18	06-Dec-18	
1032-4480	Concrete Surround for TCSS Ducting at Existing IEC bridge 8 bays (NW)	25	05-Nov-18	03-Dec-18	
1032-4490	Cover Plate for TCSS / JTI Cable Tray Existing IEC bridge (NW)	14	15-Nov-18	30-Nov-18	
1032-4520	Maintenance walkway & Fall Arrest system at Green Roof	45	15-Sep-18	09-Nov-18	
1032-4530	Remedial Works to Marine Pile Caps	21	15-Sep-18	11-Oct-18	
10.6 - Tunnel A	pproach Ramp				
	ch Ramp (Excluding Portion IIB)				
	Is & Trough Structure B,C & D	1			
1061-7160	Construct Trough Structure B Side Walls	10	18-Aug-18 A	30-Aug-18	Construct Trough Structure B Side Walls
1061-7220	Construct Trough Structure C Side Walls (2nd Pour-east part)	10	09-Aug-18 A	30-Aug-18	Construct Trough Structure C Side Walls (2
1061-7230	MJ Cover installation - Trough A/B/C Structure	6	30-Aug-18	05-Sep-18	MJ Cover installation - Trough A/B/C
1061-7240	Road, Paving & Fencing Works at Trough B/C/D	12	30-Aug-18	12-Sep-18	Rcad, Paving & Fencing Work
	Backfilling Works at Back side of Trough B & C	12	29-Aug-18	11-Sep-18	Backfilling Works at Back side
1061-7250					
1061-7250 Landscape De					
		15	09-Apr-18 A	05-Sep-18	Bay C5 > Jpstand Wall at Bay C5 (de
Landscape De	eck	15 24	09-Apr-18 A 21-Jul-18 A	05-Sep-18 15-Sep-18	Bay C5 > Jpstand Wall at Bay C5 (de
Landscape De 1061-7464	eck Bay C5 > Upstand Wall at Bay C5 (detail received on 23.07.18)		· .	· .	
Landscape De 1061-7464 1061-7477	eck Bay C5 > Upstand Wall at Bay C5 (detail received on 23.07.18) Bay C1-C5 > Type 2 Railing Above Landscape Deck (North & South side)	24	21-Jul-18 A	15-Sep-18	
Landscape De 1061-7464 1061-7477 1061-7479	eck Bay C5 > Upstand Wall at Bay C5 (detail received on 23.07.18) Bay C1-C5 > Type 2 Railing Above Landscape Deck (North & South side) Bay C1-C5 > Type 2 Railing Above Landscape Deck (East & West side) Bay C1-C5 > Waterproofing/Screeding/Root Barriers/Draining Composite/Subsoil+Soil Placing	24 35	21-Jul-18 A 18-Oct-18	15-Sep-18 27-Nov-18	
Landscape De 1061-7464 1061-7477 1061-7479 1061-7483	eck Bay C5 > Upstand Wall at Bay C5 (detail received on 23.07.18) Bay C1-C5 > Type 2 Railing Above Landscape Deck (North & South side) Bay C1-C5 > Type 2 Railing Above Landscape Deck (East & West side) Bay C1-C5 > Waterproofing/Screeding/Root Barriers/Draining Composite/Subsoil+Soil Placing	24 35	21-Jul-18 A 18-Oct-18	15-Sep-18 27-Nov-18	

Actual Work

Remaining Level of Effort
 Remaining Work

Actual Level of Effort

Critical Remaining Work ♦ ♦ Milestone

Contract HY/2009/19 Three Months Rolling Programme (20.Aug.2018 to 20.Nov.2018)

October				Novem	oer		əmber
14	21	28	04	11	18	25	02
JTI (NW)		rame	& Sign fa	ace			
P32 (NW)							
W)						1	
ing, Holdir	ng Dowr	n Bolt a	& Post			 	
rilling, Hok	ding Do	wn Bo	lt & Post	•			
ng, Holding							
8-Drilling, I	-	1		ost			
Tong Shui	-						
ਰ ਹਜੰਧੀ	., DU	, . Ja	July	0			
	Corbe	el Cons	st & Rep	lacemer	nt of Ter	nporar	y Light
						, , , , , , , , , , , , , , , , , , ,	
	_	_ [_ ·	acement			
	_		Instal	ll remain	ing stan	ndard ti	raffic 8
			►			1	
		l				1	С
							Cove
				Mainte	nance v	valkwa	y & Fa
Remedia	al Work	s to M	arine Pil	e Caps			
				-			
	_						
2nd Pour-		rt)					
Structure							
ks at Trou	igh B/C	/D					
e of Troug	hB&C					1	
etail receiv		i i					
ig Above L	andsca	ape De	eck (Nor	th & Soι	uth side)		
-		 				B	ay C1-
L		Ba	ay C1-C5	5 > Wate	erproofir	וg/Scr	eding
		 				1	
				Ря	ige 2 of 4	1	

 As phalt laying 4th Layer (C4-C5) As phalt laying 5th Layer (C4-C5) oroach Ramp Final Road Surfacing & Marking (excl Portion IIB) (C4-C5 > Noise Panel (C2-C3 > Noise Panel (C1-C5 > Railing Installations amp (Within Portion IIB) (C1 > Staircase & Ramp No. 1 instatement of Temporary Sump Pit ohalt laying 1st Layer (C1-C3) icast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (C1 > Noise Panel 	Dur 1 1 9 13 14 14 14 14 14 14 14 11 3 4 12 10 9 9 9	23-Aug-18 28-Aug-18 03-Sep-18 24-Jul-18 A 13-Jul-18 A 24-Aug-18 13-Aug-18 A 27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A 04-Sep-18	23-Aug-18 28-Aug-18 12-Sep-18 03-Sep-18 04-Sep-18 08-Sep-18 31-Aug-18 29-Aug-18 03-Sep-18 03-Sep-18 03-Sep-18			As phalt lay EB - As pha Bay Bay Bay Bay C1 Re-instate	alt layin G 1-C5 7 C2-C Bay C > Stair	Imber O 16 23 30 07 Layer (C4-C5) g 5th Layer (C4-C5) g 5th Layer (C4-C5) poroach Ramp Final Road Sur poroach Ramp Final Road Sur > Noise Panel 3 > Noise Panel -C5 > Railing Installations -C5 > Railing Installations -C5 -C5 > Railing Installatins
- As phalt laying 5th Layer (C4-C5) proach Ramp Final Road Surfacing & Marking (excl Portion IIB) (C4-C5 > Noise Panel (C2-C3 > Noise Panel (C1-C5 > Railing Installations amp (Within Portion IIB) (C1 > Staircase & Ramp No. 1 -instatement of Temporary Sump Pit phalt laying 1st Layer (C1-C3) acast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) (C1 > Noise Panel 3	1 9 13 14 14 14 11 3 4 12 10 9	28-Aug-18 03-Sep-18 24-Jul-18 A 13-Jul-18 A 24-Aug-18 13-Aug-18 A 27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	28-Aug-18 12-Sep-18 03-Sep-18 04-Sep-18 08-Sep-18 31-Aug-18 29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			As phalt lay EB - As pha Bay Bay Bay Bay C1 Re-instate	ing 4th alt layin C4-C5 7 C2-C: Bay C > Stair ement o	Layer (C4-C5) g 5th Layer (C4-C5) poroach Ramp Final Road Sur > Noise Panel 3 > Noise Panel 7 -C5 > Railing Installations case & Ramp No. 1
broach Ramp Final Road Surfacing & Marking (excl Portion IIB) (C4-C5 > Noise Panel (C2-C3 > Noise Panel (C1-C5 > Railing Installations amp (Within Portion IIB) (C1 > Staircase & Ramp No. 1 instatement of Temporary Sump Pit bhalt laying 1st Layer (C1-C3) incast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) (C1 > Noise Panel 3	9 13 14 14 14 11 3 4 12 10 9	03-Sep-18 24-Jul-18 A 13-Jul-18 A 24-Aug-18 13-Aug-18 A 27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	12-Sep-18 03-Sep-18 04-Sep-18 08-Sep-18 31-Aug-18 29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			Bay Bay Bay C1 Re-instate	C4+C5 (C2-C) Bay C > Stair	poroach Ramp Final Road Sur > Noise Panel 3 > Noise Panel - C5 > Railing Installations case & Ramp No. 1 - Temporary Sump Pit
y C4-C5 > Noise Panel y C2-C3 > Noise Panel y C1-C5 > Railing Installations amp (Within Portion IIB) y C1 > Staircase & Ramp No. 1 instatement of Temporary Sump Pit ohalt laying 1st Layer (C1-C3) acast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) y C1 > Noise Panel	13 14 14 11 3 4 12 10 9	24-Jul-18 A 13-Jul-18 A 24-Aug-18 13-Aug-18 A 27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	03-Sep-18 04-Sep-18 08-Sep-18 31-Aug-18 29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			Bay C1	<u>C</u> 4-C5 <u>y</u> C2-C: Bay C > Stair	> Noise Panel 3 > Noise Panel - C5 > Railing Installations case & Ramp No. 1 Temporary Sump Pit
v C2-C3 > Noise Panel v C1-C5 > Railing Installations amp (Within Portion IIB) v C1 > Staircase & Ramp No. 1 instatement of Temporary Sump Pit ohalt laying 1st Layer (C1-C3) iccast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) v C1 > Noise Panel	14 14 11 3 4 12 10 9	13-Jul-18 A 24-Aug-18 13-Aug-18 A 27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	04-Sep-18 08-Sep-18 31-Aug-18 29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			Bay C1	y C2-C: Bay C > Stair	3 > Noise Panel -C5 > Railing Installations case & Ramp No. 1 o Temporary Sump Pit
v C1-C5 > Railing Installations amp (Within Portion IIB) v C1 > Staircase & Ramp No. 1 instatement of Temporary Sump Pit ohalt laying 1st Layer (C1-C3) ocast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) v C1 > Noise Panel	14 11 3 4 12 10 9	24-Aug-18 13-Aug-18 A 27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	08-Sep-18 31-Aug-18 29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			Bay C1	Elay C > Stair emient (c -C5 > Railing Installations case & Ramp No. 1 c Temporary Sump Pit
amp (Within Portion IIB) y C1 > Staircase & Ramp No. 1 instatement of Temporary Sump Pit ohalt laying 1st Layer (C1-C3) incast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) y C1 > Noise Panel 3	11 3 4 12 10 9	13-Aug-18 A 27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	31-Aug-18 29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			Bay C1 Re-instate	> Stair	case & Ramp No. 1 or Temporary Sump Pit
y C1 > Staircase & Ramp No. 1 Finstatement of Temporary Sump Pit Schalt laying 1st Layer (C1-C3) Final Cover for Cable Trough & TCSS Draw Pits Final Drainage & Downpipe (within Portion IIB) Final Surfacing & Marking (within Portion IIB) (after CC installation works) Y C1 > Noise Panel	3 4 12 10 9	27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			Re-instate	ement (o Temporary Sump Pit
instatement of Temporary Sump Pit ohalt laying 1st Layer (C1-C3) ccast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) r C1 > Noise Panel	3 4 12 10 9	27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			Re-instate	ement (o Temporary Sump Pit
instatement of Temporary Sump Pit ohalt laying 1st Layer (C1-C3) ccast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) r C1 > Noise Panel	3 4 12 10 9	27-Aug-18* 30-Aug-18 09-Jul-18 A 16-Jul-18 A	29-Aug-18 03-Sep-18 01-Sep-18 30-Aug-18			Re-instate	ement (o Temporary Sump Pit
<pre>bhalt laying 1st Layer (C1-C3) ccast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) / C1 > Noise Panel 3</pre>	4 12 10 9	30-Aug-18 09-Jul-18 A 16-Jul-18 A	03-Sep-18 01-Sep-18 30-Aug-18		Ļ			
<pre>bhalt laying 1st Layer (C1-C3) ccast Cover for Cable Trough & TCSS Draw Pits ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) / C1 > Noise Panel 3</pre>	4 12 10 9	30-Aug-18 09-Jul-18 A 16-Jul-18 A	03-Sep-18 01-Sep-18 30-Aug-18					
ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) v C1 > Noise Panel	12 10 9	09-Jul-18 A	01-Sep-18 30-Aug-18		◄ ا	Aspl	ha <mark>lt lay</mark> i	ing tet Lover (Ct C2)
ad Drainage & Downpipe (within Portion IIB) ad Surfacing & Marking (within Portion IIB) (after CC installation works) v C1 > Noise Panel	10 9	16-Jul-18 A	30-Aug-18	_				
ad Surfacing & Marking (within Portion IIB) (after CC installation works) v C1 > Noise Panel	9					Preca	st Cove	er for Cable Trough & TCSS D
v C1 > Noise Panel		04-Sep-18				Road Dr	ainage	& Downpipe (within Portion IIE
3	9		13-Sep-18	_				Road Surfacing & Marking (wit
		27-Jul-18 A	03-Sep-18			Bay	<u>C</u> I > N	loise Panel
Road 13 (South 2 - Adi to Car Park) Backfilling & Compaction								
	6	05-Jul-18 A	25-Aug-18		Sli	p Road 13 ((South	2 - Adj to Car Park) Backfilling
Road 13 (South 2 - Adj to Car Park) Road Kerb & Other Misc Works	9	23-Aug-18	01-Sep-18	_	└ ►	Slip Ro	bad 13	(South 2 - Adj to Car Park) Ro
Road 13 (West - Near Site Office) TCSS, Draw Pits & other Civil Provision	5	07-Jun-18 A	24-Aug-18	_	Slip	Road 13 (\	Nest -	Near Site Office) TCSS, Draw
Road 13 (West - Near Site Office) Trimming Ex Surface & Drainage	8	07-Jun-18 A	28-Aug-18	_		Slip Road	13 (We	st - Near Site Office) Trimming
Road 13 (West - Near Site Office) Backfilling & Compaction	6	24-Aug-18	30-Aug-18	-		Slip Roa	d 13 (V	Vest - Near Site Office) Backfi
Road 13 (West - Near Site Office) Road Kerb & Other Misc Works	8	29-Aug-18	06-Sep-18		I ⊸I	S	Slip Roa	d 13 (West - Near Site Office)
Road 13 (North - Sea Side) Drainage & Other Undergroud Civil Provision	10	21-Jul-18 A	31-Aug-18			Slip Ro	ad 13 (North - Sea Side) Drainage &
Road 13 (North - Sea Side) Backfilling & Compaction	6	30-Aug-18	05-Sep-18	_	┡	Sli	ip Road	13 (North - Sea Side) Backfil
Road 13 (North - Sea Side) Road Kerb & Other Misc Works	8	04-Sep-18	12-Sep-18	_			s s	lip Road 13 (North - Sea Side)
Road Surfacing	7	07-Sep-18	14-Sep-18					Slip Road Surfacing
ad Marking, Fencing, Footpath Paver & Other Finishing Works	7	07-Sep-18	14-Sep-18					Road Marking, Fencing, Foot
iscellaneous Works								
M Stage 10 - TTM Enabling Works	1	14-Sep-18	14-Sep-18				. <mark> +</mark> ₽	TTM Stage 10 - TTM Enabling
M Stage 10 - Tunnel Commisioning	0		14-Sep-18	_			•	TM Stage 10 - Tunnel Comn
atson Road (Portion III)			,			· - ±		L
e-cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid	18	10-May-18 A	08-Sep-18				Pre-c	ast Clay Paving EVA to EVB (r
OF THE WORKS								
fort Bemaining Work			~	ontro		0000/10		
							0040	
	Road 13 (North - Sea Side) Road Kerb & Other Misc Works Road Surfacing d Marking, Fencing, Footpath Paver & Other Finishing Works scellaneous Works A Stage 10 - TTM Enabling Works A Stage 10 - Tunnel Commisioning tson Road (Portion III) cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid	Road 13 (North - Sea Side) Backfilling & Compaction 6 Road 13 (North - Sea Side) Road Kerb & Other Misc Works 8 Road Surfacing 7 d Marking, Fencing, Footpath Paver & Other Finishing Works 7 scellaneous Works 1 M Stage 10 - TTM Enabling Works 1 M Stage 10 - Tunnel Commisioning 0 ntson Road (Portion III) 0 cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid 18 F THE WORKS 18 ort Remaining Work	Road 13 (North - Sea Side) Backfilling & Compaction 6 30-Aug-18 Road 13 (North - Sea Side) Road Kerb & Other Misc Works 8 04-Sep-18 Road Surfacing 7 07-Sep-18 d Marking, Fencing, Footpath Paver & Other Finishing Works 7 07-Sep-18 scellaneous Works 7 07-Sep-18 M Stage 10 - TTM Enabling Works 1 14-Sep-18 M Stage 10 - Tunnel Commisioning 0 0 tson Road (Portion III) 1 14-Sep-18 cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid 18 10-May-18 A F THE WORKS 7 07 ort Remaining Work 1	Road 13 (North - Sea Side) Backfilling & Compaction 6 30-Aug-18 05-Sep-18 Road 13 (North - Sea Side) Road Kerb & Other Misc Works 8 04-Sep-18 12-Sep-18 Road Surfacing 7 07-Sep-18 14-Sep-18 d Marking, Fencing, Footpath Paver & Other Finishing Works 7 07-Sep-18 14-Sep-18 scellaneous Works 7 07-Sep-18 14-Sep-18 M Stage 10 - TTM Enabling Works 1 14-Sep-18 14-Sep-18 M Stage 10 - Tunnel Commisioning 0 14-Sep-18 ntson Road (Portion III) 14-Sep-18 14-Sep-18 rcast Clay Paving EVA to EVB (remaining paver to arrive on site by mid 18 10-May-18 A 08-Sep-18 F THE WORKS C	Road 13 (North - Sea Side) Backfilling & Compaction 6 30-Aug-18 05-Sep-18 Road 13 (North - Sea Side) Road Kerb & Other Misc Works 8 04-Sep-18 12-Sep-18 Road Surfacing 7 07-Sep-18 14-Sep-18 d Marking, Fencing, Footpath Paver & Other Finishing Works 7 07-Sep-18 14-Sep-18 scellaneous Works 1 14-Sep-18 14-Sep-18 A Stage 10 - TTM Enabling Works 1 14-Sep-18 14-Sep-18 A Stage 10 - TUNNEl Commissioning 0 14-Sep-18 14-Sep-18 A Stage 10 - Tunnel Commissioning 0 14-Sep-18 14-Sep-18 A Stage 10 - TUNNEl Commissioning 0 14-Sep-18 14-Sep-18 A Stage 10 - TUNNEl Commissioning 0 14-Sep-18 14-Sep-18 A Stage 10 - TUNNEl Commissioning 0 0 14-Sep-18 A Stage 10 - TUNNEl Commissioning 0 0 08-Sep-18 Cast Clay Paving EVA to EVB (remaining paver to arrive on site by mid 18 10-May-18 A 08-Sep-18 F THE WORKS Remaining Work Critical Remaining Work Contraction Contraction Contraction Contraction Contracting Work Contraction Contraction Contracti	Road 13 (North - Sea Side) Backfilling & Compaction 6 30-Aug-18 05-Sep-18 Road 13 (North - Sea Side) Road Kerb & Other Misc Works 8 04-Sep-18 12-Sep-18 Road Surfacing 7 07-Sep-18 14-Sep-18 d Marking, Fencing, Footpath Paver & Other Finishing Works 7 07-Sep-18 14-Sep-18 scellaneous Works 1 14-Sep-18 14-Sep-18 M Stage 10 - TTM Enabling Works 1 14-Sep-18 14-Sep-18 M Stage 10 - Tunnel Commisioning 0 14-Sep-18 rcsat Clay Paving EVA to EVB (remaining paver to arrive on site by mid 18 10-May-18 A 08-Sep-18 F THE WORKS Image Remaining Work Image Remaining Work Image Remaining Work Image Remaining Work Image Remaining Work	Road 13 (North - Sea Side) Backfilling & Compaction 6 30-Aug-18 05-Sep-18 Road 13 (North - Sea Side) Road Kerb & Other Misc Works 8 04-Sep-18 12-Sep-18 Road Surfacing 7 07-Sep-18 14-Sep-18 d Marking, Fencing, Footpath Paver & Other Finishing Works 7 07-Sep-18 14-Sep-18 scellaneous Works 1 14-Sep-18 14-Sep-18 A Stage 10 - TTM Enabling Works 1 14-Sep-18 14-Sep-18 A Stage 10 - Tunnel Commisioning 0 14-Sep-18 A Stage 10 - Tunnel Commisioning 0 14-Sep-18 rcast Clay Paving EVA to EVB (remaining paver to arrive on site by mid 18 10-May-18 A 08-Sep-18 F THE WORKS Contract HY/2009/19 ort Remaining Work Critical Remaining Work Contract HY/2009/19	Road 13 (North - Sea Side) Backfilling & Compaction 6 30-Aug-18 05-Sep-18 Road 13 (North - Sea Side) Road Kerb & Other Misc Works 8 04-Sep-18 12-Sep-18 Road Surfacing 7 07-Sep-18 14-Sep-18 d Marking, Fencing, Footpath Paver & Other Finishing Works 7 07-Sep-18 14-Sep-18 scellaneous Works 1 14-Sep-18 14-Sep-18 A Stage 10 - TTM Enabling Works 1 14-Sep-18 14-Sep-18 A Stage 10 - TTM Enabling Works 0 14-Sep-18 reast Clay Paving EVA to EVB (remaining paver to arrive on site by mid) 18 10-May-18 A 08-Sep-18 F THE WORKS Contract HY/2009/19

October 14 21	28	2	04	Novem	1ber	25	ember
	2	<u>ر</u>	04		10	20	
							, , , ,
urfacing & Ma	arking (exc	l Porti	on IIB)			
							1 1 1
							1 1 1
							1 1 1
							1 1 1 1
Draw Pits							
B)							1 1 1
ithin Portion I	llB) (aft	er (CC ins	tallation	works)		, , , ,
) (a.t			tallation			1 1 1
g & Compac	tion						; !
oad Kerb & C		ico	Mork	^			
				5			, , , ,
v Pits & other							
g Ex Surface	e & Dra	inaç	ge Wo	rks			1 1 1 1
filling & Comp	paction						1 1 1 1
e) Road Kerb	& Othe	r M	lisc W	orks			! ! !
Other Under	rgroud	Civi	l Prov	sion Wo	orks		, , , ,
illing & Comp	action						
) Road Kerb		r M	isc W	orke			1
TICAU NEID		ı ivi	130 11	UINO			1 1 1
tpath Paver 8	& Other	Fir	nishing	Works			
ng Works							1 1 1
-							
misioning							
remaining pa	war ta a	rriv					
remaining pa		ai i i V		one by II	nu Aug)		
							I I
				Р	age 3 of	4	

Activity ID	Activity Name	Rem	Start	Finish									2018	
		Dur			August				Se	eptembe				Oct
					12	19	26	02	0	9 16	6 23	30	07	
11.0 - Portion	XIIC						_	1			-			
1110-2500	EB - Modification of Road Marking at Hing Fat Slip Road (Night Work)	4	05-Sep-18*	08-Sep-18					Ē	3 - Modi	ication of	Road	Marking) at I
11.1 - Portion	XIIA - Stage 1													
11.1.1 - Along	y Watson Road - Waterwork & Roadworks (Portion XIIA)													
1110-2853	Road Public Lighting at Watson Road	9	09-Aug-18 A	29-Aug-18				Road F	Publio	Lighting	at Watso	n Roa	d	
1110-2857	Installation of Pillar Box for Bridge D & E	11	18-Aug-18 A	31-Aug-18				Insta	allation	of Pillar	Box for E	Bridge	D & E	
1110-2859	Road Fencing / Street Furniture at Watson Road	12	01-Sep-18	14-Sep-18			Ļ			🗖 Roa	d Fencin	g / Stre	eet Furn	iture
11.1.4 - Footi	ng and frame/pole for directional sign FVMSH2, ADS16 and OHVD (Portion XI	IA)						-+						
1110-2989	Reinstatement of Footpath near FVMSH2 (currently occupied by China State & Leigthton)	11	13-Aug-18 A	31-Aug-18				🛛 Rein	istaten	nent of F	ootpath r	near F	VMSH2	(cur
11.2 - Portion	XIIA - Stage 2 - Along Gordon House - Cross road ducting at Hing Fat S	t (public	chol)						İ					
1110-3020	Miscellaneous Road Works at Portion XIIA (5 TTA - works only on Sun & PH; 12d)(under discussion bet AECOM & TD)	23	18-Aug-18 A	14-Sep-18		•	!			Mis Mis	cellaneou	s Roa	d Works	; at l
11.3 - Portion	XIIA - Stage 3 - Preparation & works night before road opening													
1110-3030	Misc Works prior to CWB opening incl preparation - Stage 2	12	30-Aug-18	12-Sep-18*			۲		1-	Misc	Norks pr	or to C	CWB ope	enin

Actual Level of Effort Actual Work

♦ ♦ Milestone

Contract HY/2009/19 Three Months Rolling Programme (20.Aug.2018 to 20.Nov.2018)

8								
	October				Novem	ber	:	ember
7	14	21	28	04	11	18	25	02
ig a	at Hing I	Fat Silp	Road (I	Night W	ork)			
			1				1	
nit	ure at W	lateon	Boad					
. /							, i	
2 (0	currently	/ occup	ied by C	china St	ate & Lo	eigthton)	
~	at Dartia		ς τ τ λ	worko	onlyon	Sup 9	- 	1)(upd
.5	at Portic		STIA-	WUIKS	Only On	Suna	РП, IZU :	i)(unu
oer	ning incl	prepar	ation - S	Stage 2				
	-	<u> </u>		-				
					Pa	ige 4 of	4	
				1				

SR8_DWP_R08-02	MU63				SR	8 - Layout for 3N	/RP_2	108_06								
Activity ID	Activity Name	Original Duration	Start	Finish									2018			_
Total		2356d	21-Mar-13 A	01-Sep-19		Jun					Jul				Aug	-
	Update Progress As of 20 Jun 18	2356d	21-Mar-13 A	01-Sep-19												+
	include Re-provisioning Works of KD4,KD5)	247d	30-Jan-18 A	23-Sep-18												-
External Works		151d	30-Jan-18 A	17-Sep-18												+
Zone 1		60d	18-Apr-18 A	27-May-18 A		I I I I I I I I I I I I I I										+
Drainage Align	ment Confirmation for MH72, 73, 74 due to Tree T1106	60d	18-Apr-18 A	27-May-18 A		1 I I I I I I I I I I I I I I I I I I I										+
EXW_1155	Confirmation, TTA application and construction of re-routing of drainage works near RW8E	60d	18-Apr-18 A	27-May-18 A	TA appl	ication and construct	ton of re-	-routing of	drainage wor	ks near RW8	Eside					
Zone 4 up to Ele	side Jerly Facilities	125d	30-Jan-18 A	17-Sep-18												
Elderly Facilitie	ss V/039 Received on 22 Jun 2017	100d	30-Jan-18 A	17-Sep-18												+
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	13-Aug-18											Facilitie	ə\$ fa
EXW_2280	Ground levelling, drainage works and safety met installation	30d	14-Aug-18	17-Sep-18	_											<u> </u>
Additional Wal	kway & Arbour V/040 Received on 22 Aug 2017	93d	28-Mar-18 A	28-Jul-18												+
EXW_2310	Assiciated drainage works for the walkway	20d	28-Mar-18 A	23-May-18 A	rks for	he walkway										
EXW_2320	Arbour installation and walkway construction	30d	03-May-18 A	28-Jul-18									Arbour insta	allation and wa	lkway const	ruct
Reverting Traffi	c for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)	164d	26-Mar-18 A	23-Sep-18		1 I 1 I 1 I 1 I 1 I 1 I 1 I 1 I										+
TTA Revert Traf	fic Back to Original Alignment	105d	26-Mar-18 A	28-Jul-18		I I I I I I I I I I										+
East Bound TT	A - IEC East Bound, Victoria Park Road & footpath along Sea Side	93d	28-Mar-18 A	28-Jul-18		1 I 1 I 1 I 1 I 1 I 1 I 1 I 1 I										t
TTM Stage 1 -	IEC (East Bound)	6d	21-Jun-18	26-Jun-18		I I I I I I I I I I I I										+
Reinstatemtr	nent Existing Structure	6d	21-Jun-18	26-Jun-18		1 I I I I I I I I I I I I I I I I I I I										
EB_1020	Install metal parapet on parapet wall (30m)	6d	21-Jun-18	26-Jun-18				Instal	l metal parap	et on parapet	wall (30m)					
TTM Stage 2 -	Revert Traffiic back to Original Victoria Road	4d	27-Jun-18	30-Jun-18												1
Existing Brid	ge Pararpet Reinstatement	4d	27-Jun-18	30-Jun-18												1
EB_1180	Install metal parapet on parapet wall (40m)	4d	27-Jun-18	30-Jun-18					Install met	al parapet on	parapet wall	(40m)				
TTM Stage 3 -	Reinstatement of Footpath along Seafront	93d	28-Mar-18 A	28-Jul-18												Ť
Reinstateme	nt of Existing Utilities at Existing Footpath	86d	28-Mar-18 A	24-Jul-18												
EB_1600	Lay HGC, PCCW, Whart T&T and NWT telecom ducts and construct drawpits	10d	28-Mar-18 A	24-Jul-18								Lay H	IGC, PCCW, \	Whart T&T and	NWT telec	om
EB_1620	Reinstate permanent water main	5d	18-Apr-18 A	17-Jul-18							Reir	nstate permane	nt water main			
EB_1580	Water main Connection by WSD	2d	20-Jun-18 A	20-Jun-18 A			Water	main Con	nection by W	SD						
Reinstateme	nt of Permanent Footpath at Seafront	49d	27-May-18 A	26-Jul-18												
EB_1630	Backfilling Subbase	3d	27-May-18 A	29-May-18 A	ubbase											
EB_1640	Concreting of Permanent Footpath	4d	29-May-18 A	25-Jul-18								Cor	creting of Per	manent Footp	ath	
EB_1650	Pedestrian diversion on Permanent Footpath	1d	26-Jul-18	26-Jul-18								∎ P	edestrian dive	rsion on Perm	anent Footp	ath
Reinstateme	nt Works in Traffic Deck Part B	3d	07-May-18 A	28-Jul-18												
EB_1700	Backfill Type B Material up to 2m below F.F.L (Compaction by proof rolling method of 0.2m each layer)	3d	07-May-18 A	28-Jul-18									Backfill Type	e B Material up	to 2m below	v F.
West Bound - I	EC West Bound & Tsing fung Street	74d	26-Mar-18 A	06-Jul-18												
TTM Stage 2 -	Revert Traffic back to Original Tsing Fung Street	5d	21-Jun-18	25-Jun-18												
Existing Brid	ge Pararpet Reinstatement	5d	21-Jun-18	25-Jun-18												
IECW_1140		5d	21-Jun-18	25-Jun-18				Install r	netal parapet	on parapet w	all (60m)					
	Reinstatement of Victoria Park	21d	26-Mar-18 A	06-Jul-18												_
	nt Works inside Victoria Park	21d	26-Mar-18 A	06-Jul-18												
IECW_1470		21d	26-Mar-18 A	06-Jul-18						Slope Reins	tatement of V	ictoria Park				_
· · · · · · · · · · · · · · · · · · ·	Minor Outstanding / Remaining Works for KD9	110d	18-May-18 A	23-Sep-18												-
East Bound - M	linor Outstanding Works in Footpath after Substantial Completion of KD9	88d	18-May-18 A	01-Sep-18												

中國連幕工程(**香港)**有限公司 CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

Actual Work Remaining Work

Critical Remaining Work

Page 1 of 3

Milestone

Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Progamme

						A	ppendix	C.5
Aug						Sep		
	s fabrication							
aciiile	STADICATION							
							Ground	levellin
constr	uction							
r telecr	m ducts and	construct d	a	wnits				
101000			u	inplie				
Footpa	ath							
			-					
h below	F.F.L (Compa	iction by pro	0	f rolling me	tho	d of 0.2m eac	h layer)	
	1							
	1		_					
			_					
		evision				Checked	Approv	ed
DW	/P-08 (2) -	3 Months	R	lolling	Т	L	TL	


Date

20-Jun-18

D	Activity Name	Original	Start	Finish							
		Duration			Ju	ŋ		, Ju	2018		8
	tement Works for Existing Sign Gantry	75d	30-May-18 A	27-Aug-18							
EB_1750	Laying Public Lighting duct	3d	30-May-18 A	25-Aug-18							
EB_1780	Erect Sign Gantry Steel Supports and Sign Gantry Beam across VPR and IEC E/B	4d	29-Jul-18	01-Aug-18					Er	ect Sign Gantry	y Steel
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	02-Aug-18	02-Aug-18					•	Installation of E	. & M a
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	26-Aug-18	27-Aug-18							
Minor Reinstat	tement Works for Central Median of IEC & Footbridge	6d	02-Aug-18	07-Aug-18							
EB_1800	Reconstruction of central divider (6m long, night work)	6d	02-Aug-18	07-Aug-18						Recor	nstruc
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	03-Aug-18	03-Aug-18					•	Dismantlemer	nt of t
Minor Reinstat	tement Works for Footpath	88d	18-May-18 A	01-Sep-18							
EB_1820	Place kerbline along VPR footpath	3d	18-May-18 A	23-Aug-18							-
EB_1850	Backfilling subbase material	2d	27-May-18 A	29-May-18 A	ubbase material	-					
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	24-Aug-18	24-Aug-18	_						
EB_1840	Re-provision of Tree	8d	25-Aug-18	01-Sep-18							
Minor Reinstat	tement Works for Bus Stop	56d	23-May-18 A	29-Aug-18							
EB_1860	Reinstatement of Permanent Bus Stop	5d	23-May-18 A	26-Jun-18 A			Reinstatement of P	ermanent Bus; Sto	p		
EB_1870	Relocation of Bus Stop	1d	27-Jun-18 A	27-Jun-18 A			Relocation of Bus	Stop			
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5d	25-Aug-18	29-Aug-18	_						
	tement Works for Loop Detector	4d	04-Aug-18	07-Aug-18							
EB_1900	Construction of concrete plinth and fix counter housing for Loop Detector (ILDS)	3d	04-Aug-18	06-Aug-18						Constru	uction
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	07-Aug-18	07-Aug-18	_					E&W	
	Completion of Minor Outstanding / Remaining Works for KD9	95d	21-Jun-18	23-Sep-18							
	tement Works for Victoria Park	37d	07-Jul-18	12-Aug-18							
IECW_1500	Re-provision of Tree	32d	07-Jul-18	07-Aug-18	_					Re-pr	1
IECW_1510	Laying Irrigation Main	10d	22-Jul-18	31-Jul-18	_				Layır	ng Irrigation Ma	
IECW_1520	Construct Landscape Footpath and Lightings	7d	06-Aug-18	12-Aug-18							
	tement Works in IEC West Bound	95d	21-Jun-18	23-Sep-18							
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	21-Jun-18	28-Jun-18			Replacement o	f new movement jo	oint at IEC W/B (Sun midnight only)		
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun midnight only)	57d	29-Jun-18	24-Aug-18							
IECW_1640	Erection of new precast concrete panels (12 nos.) at abutment M facing to VPR	2d	25-Aug-18	26-Aug-18							
IECW_1620	Repairing of concrete defects on extg concrete deck and abutment M	30d	25-Aug-18	23-Sep-18							
orks in Victori	ia Park (KD4, KD5, KD9)	169d	01-Mar-18 A	07-Aug-18							
e-Provisioning	Works	169d	01-Mar-18 A	07-Aug-18							
Nursery Compo	ound	169d	01-Mar-18 A	07-Aug-18							
Nursery compo	ound	169d	01-Mar-18 A	07-Aug-18							
ABWF		27d	05-Apr-18 A	07-Aug-18							
Metal Fence		27d	05-Apr-18 A	07-Aug-18							
VP_NC_182	20 Installation	30d	05-Apr-18 A	07-Aug-18		-				Install	Ilatio
Fire Srevices		14d	21-Jun-18	07-Jul-18							
	FS inspection	14d	21-Jun-18	07-Jul-18				FS inspection			
Plimbing and	I Flushing Water Supplies	14d	21-Jun-18	07-Jul-18							
VP_NC_2100		14d	21-Jun-18	07-Jul-18				WSD Inspectior	n		
	ks Aside Nursery Compound	56d	01-Mar-18 A	14-Jul-18							
	rks Around Nursery Compound	56d	01-Mar-18 A	14-Jul-18							
		500									1
				Dent	of 0					Date	te
	Actual W	Vork ing Work		Page 2	013					20-Jun-1	
	『連幕工程(春港) 斉腹公司 Remaining Critical F	ma Mark		1							-

		Α	ppendix C.5
		Sep	
Laying	Public Lighting	duct	
orts and Sign Gantry Be	am across VPF	R and IEC E/B	
Gantry (night work)			
🗖 Co	nnection of Pub	lic Lighting by Hy	D (Lighting)
central divider (6m long	, night work)		
ectional sign mounted o	n extg footbride	ge	
Place kerb	ine along VPR	footpath	
Reinstate	ment of Distric	t Council Welcon	ne Sign and opening
		sion of Tree	0 0
	Painstate Plan	tor(Provious Tor	porary Bus Stop)
	Ttell)State F lan		iporary bus diop)
vote plinth and fiv equal	ion housing for	Logn Detector (II	
rete plinth and fix coun			
statement of Loop Dete	ector (ILDS) by	EMSD (night wo	гк)
e -			
t Landscape Footpath	and Lightings		
Repairing	of extg conc o	leck surface afte	r milling of temp asp
Erect	ion of new pred	cast concrete par	nels (12 nos.) at abu
			Re
1 i		1	. :
Revision		Checked	Approved
VP-08 (2) - 3 Montl	ns Rolling	TL	TL

SR8	_DWP_R08-02 M	J63				SR8 - Layout for 3MRP_2108_06
Activi	ty ID	Activity Name	Original Duration	Start	Finish	2018 Jun Jul Aug
	VP_NC_2250	Reinstatement of Existing Boundary Fence Wall Around Nursery Compound	45d	01-Mar-18 A	26-May-18 A	Existing Boundary Fence Wall Around Nursery Compound
	VP_NC_2260	EVA Construction	15d	28-May-18 A	14-Jul-18	EVA Construction
	KD11, KD12, KD13	KD18 Establishment Works for Landscape Softworks	390d	08-Aug-18	01-Sep-19	
	KD11 - Section 7A	Portion XIV & XV (Victoria Park Open Space)	365d	08-Aug-18	07-Aug-19	
	EW_1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	08-Aug-18	07-Aug-19	
	KD13 - Section 7C	: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)	365d	02-Sep-18	01-Sep-19	
	EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	02-Sep-18	01-Sep-19	
	KD18 - Section 11:	Transplanted Trees DBH>500mm in Portion VA and XII	365d	08-Aug-18	07-Aug-19	
	EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA. XII	365d	08-Aug-18	07-Aug-19	
	KD10 - Preservatio	n and Protection of Trees	1088d	21-Mar-13 A	27-Sep-18	
	PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	27-Sep-18	
	KD15 & KD8 - Moo	ing Components Upkeep (CBTS and ATS)	979d	15-May-14 A	21-Jun-18	
	MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Jun-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS



		Appen	dix C.5
		Sep	
Revision	Chec		proved

Revision	Checked	Approved
NP-08 (2) - 3 Months Rolling	TL	TL

ID	Activity Name	Original		Finish	
		Duration			2018 Sep Oct
tal		2421d	21-Mar-13 A	05-Nov-19	
WP-08 - (2) -	- Update Progress As of 20 Sep 18	2421d	21-Mar-13 A	05-Nov-19	
orks in KD9 (l	nclude Re-provisioning Works of KD4,KD5)	339d	30-Jan-18 A	24-Dec-18	8
xternal Works	s Under KD9	178d	30-Jan-18 A	20-Dec-18	8
Zone 4 up to El	Iderly Facilities	178d	30-Jan-18 A	20-Dec-18	8
Elderly Faciliti	es V/039 Received on 22 Jun 2017	178d	30-Jan-18 A	20-Dec-18	8
EXW_2270	Facilities fabrication	90d	30-Jan-18 A	15-Nov-18	8
EXW_2280	Ground levelling, drainage works and safety met installation	30d	16-Nov-18	20-Dec-18	8
Additional Wa	Ikway & Arbour V/040 Received on 22 Aug 2017	30d	03-May-18 A	31-Oct-18	3
EXW_2320	Arbour installation and walkway construction	30d	03-May-18 A	31-Oct-18	8 Arbour installation and
everting Traff	ic for IEC,VP Rd & TF St & Seawall Reinstatement (KD9)	256d	13-Apr-18 A	24-Dec-18	8
TTA Revert Traf	ffic Back to Original Alignment	171d	13-Apr-18 A	04-Oct-18	3
East Bound T	TA - IEC East Bound, Victoria Park Road & footpath along Sea Side	10d	21-Sep-18	30-Sep-18	8
TTM Stage 1	- IEC (East Bound)	6d	21-Sep-18	26-Sep-18	8
Reinstatemt	ment Existing Structure	6d	21-Sep-18	26-Sep-18	
EB_1020	Install metal parapet on parapet wall (30m)	6d	21-Sep-18	26-Sep-18	
	- Revert Traffiic back to Original Victoria Road	4d	27-Sep-18	30-Sep-18	
-	dge Pararpet Reinstatement	4d	27-Sep-18	30-Sep-18	
EB_1180	Install metal parapet on parapet wall (40m)	4d	27-Sep-18	30-Sep-18	
	IEC West Bound & Tsing fung Street	166d	13-Apr-18 A	04-Oct-18	
-	- Revert Traffic back to Original Tsing Fung Street	5d	21-Sep-18	25-Sep-18	
	dge Pararpet Reinstatement	5d	21-Sep-18	25-Sep-18	
IECW_1140		5d	21-Sep-18	25-Sep-18	
	- Reinstatement of Victoria Park	21d	13-Apr-18 A	04-Oct-18	
Reinstateme	ent Works inside Victoria Park	21d	13-Apr-18 A	04-Oct-18	
IECW_1470	Slope Reinstatement of Victoria Park	21d	13-Apr-18 A	04-Oct-18	8 Slope Reinstatement of Victoria Park
completion of	Minor Outstanding / Remaining Works for KD9	200d	03-May-18 A	24-Dec-18	8
East Bound - I	Minor Outstanding Works in Footpath after Substantial Completion of KD9	150d	18-May-18 A	08-Oct-18	
Minor Reinsta	atement Works for Existing Sign Gantry	3d	14-Sep-18 A	19-Sep-18 A	3A
EB_1760	Connection of Public Lighting by HyD (Lighting)	2d	14-Sep-18 A	18-Sep-18 A	8 A Connection of Public Lighting by HyD (Lighting)
EB_1790	Installation of E & M at Sign Gantry (night work)	1d	19-Sep-18 A	19-Sep-18 A	8 A Installation of E & M at Sign Gantry (night work)
Minor Reinsta	atement Works for Central Median of IEC & Footbridge	6d	01-Oct-18	06-Oct-18	
EB_1800	Reconstruction of central divider (6m long, night work)	6d	01-Oct-18	06-Oct-18	8 Reconstruction of central divider (6m long, night work)
EB_1810	Dismantlement of temp directional sign mounted on extg footbridge	1d	01-Oct-18	01-Oct-18	8 Dismantlement of temp directional sign mounted on extg footbridge
Minor Reinsta	atement Works for Footpath	150d	18-May-18 A	08-Oct-18	
EB_1820	Place kerbline along VPR footpath	3d	18-May-18 A	17-Sep-18 A	8 A Place kerbline along VPR footpath
EB_1840	Re-provision of Tree	8d	27-Sep-18 A	08-Oct-18	8 Re-provision of Tree
EB_1830	Reinstatement of District Council Welcome Sign and opening plaque at Planter area	1d	03-Oct-18 A	03-Oct-18 A	8 A Reinstatement of District Council Welcome Sign and opening plaque at Plant
Minor Reinsta	atement Works for Bus Stop	5d	20-Jul-18 A	05-Oct-18	
EB_1880	Reinstate Planter(Previous Temporary Bus Stop)	5d	20-Jul-18 A	05-Oct-18	
	atement Works for Loop Detector	1d	23-Aug-18 A	24-Aug-18 A	
EB_1890	E&W work for Reinstatement of Loop Detector (ILDS) by EMSD (night work)	1d	23-Aug-18 A	24-Aug-18 A	
LD_1030	Lass work for removalement of Loop Delector (1100) by ENOD (11911 WOR)	iu iu	20 Aug-10 A	2	(ingrit work)

	Actual Work	Page 1 of 2	Date	
	Remaining Work		20-Sep-18	DWP-0
中國連幕工程(春港)有限公司	Critical Remaining Work	Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip		
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.	Milestone	Road 8 Section) - 3 Months Rolling Progamme		

				Α	ppendix	C.5
lov				Dec		
Fa	cilities fabrica	ttion				
					Gi	round l
way	construction					
					1 1 1	
		 			1 1 1 1	
					1 1 1 1	
					1 1 1 1	
		 			1 1 1 1	
		 			1 1 1 1	
		1 1 1 1				
					1	
					1 1 1	
ea						
					1 1 1 1	
					1 1 1 1	
		evision		Checked	Approv	<u>ad</u>
DW	، (P-08 (2)	3 Months	Rolling	TL	TL	u
				-		

8_DWP_R08-02 N	MU66				SR8 - Layout for 3MRP_2108_09
vity ID	Activity Name	Original Duration	Start	Finish	2018
					Sep Oct Nov
	ement Works for Victoria Park	83d	03-May-18 A	05-Nov-18	
IECW_1500	Re-provision of Tree	32d	03-May-18 A	05-Nov-18	Re-provision of Tree
IECW_1510	Laying Irrigation Main	10d	27-Sep-18 A	14-Oct-18	Laying Irrigation Main
IECW_1520	Construct Landscape Footpath and Lightings	7d	20-Oct-18	26-Oct-18	Construct Landscape Footpath and Lig
Minor Reinstate	ement Works in IEC West Bound	95d	21-Sep-18	24-Dec-18	
IECW_1600	Replacement of new movement joint at IEC W/B (Sun midnight only)	8d	21-Sep-18	28-Sep-18	Replacement of new movement joint at IEC W/B (Sun midnight only)
IECW_1610	Repairing of extg conc deck surface after milling of temp asphalt at IEC W/B and E/B (Sun	57d	29-Sep-18	24-Nov-18	
IECW_1620	midniaht only) Repairing of concrete defects on extg concrete deck and abutment M	30d	25-Nov-18	24-Dec-18	
Works in Victoria	a Park (KD4, KD5, KD9)	185d	05-Apr-18 A	09-Nov-18	
Re-Provisioning	Works	185d	05-Apr-18 A	09-Nov-18	
Nursery Compo	und	185d	05-Apr-18 A	09-Nov-18	
Nursery compo	bund	185d	05-Apr-18 A	09-Nov-18	
ABWF		27d	05-Apr-18 A	09-Nov-18	
Metal Fence		27d	05-Apr-18 A	09-Nov-18	
VP_NC_1820	Installation	30d	05-Apr-18 A	09-Nov-18	
Fire Srevices		14d	20-Aug-18 A	09-Oct-18	
VP_NC_2030	FS inspection	14d	20-Aug-18 A	09-Oct-18	FS inspection
	3, KD18 Establishment Works for Landscape Softworks	365d	06-Nov-18	05-Nov-19	
	A: Portion XIV & XV (Victoria Park Open Space)	365d	06-Nov-18	05-Nov-19	
EW 1012	Establishment Works - for Landscape Softworks and transplanted trees in Portion XV	365d	06-Nov-18	05-Nov-19	
				05-Nov-19	
	C: Portion IVA, VA, VIII, IX, XII (excl. DBH>500mm)	365d	06-Nov-18		
EW_1040	Establishment Works - for Landscape Softworks and transplanted trees in Portion IVA, VA, VIII, IX, XII excl. DBH>500mm	365d	06-Nov-18	05-Nov-19	
	1: Transplanted Trees DBH>500mm in Portion VA and XII	365d	06-Nov-18	05-Nov-19	
EW_1050	Establishment Works - for Landscape Softworks and transplanted trees DBH>500mm in Portion VA, XII	365d	06-Nov-18	05-Nov-19	
KD10 - Preservati	ion and Protection of Trees	1088d	21-Mar-13 A	28-Dec-18	
PPT_0000	Preservation and Protection of Existing Trees	1088d	21-Mar-13 A	28-Dec-18	
KD15 & KD8 - Mo	oring Components Upkeep (CBTS and ATS)	979d	15-May-14 A	21-Sep-18	
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979d	15-May-14 A	21-Sep-18	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS

中国連幕工程(春港) 余限公司 CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

Actual Work Remaining Work Critical Remaining Work Milestone

Page 2 of 2

20-Sep-18 Contract No. HY/2010/08: Central - Wanchai Bypass Tunnel +(Slip Road 8 Section) - 3 Months Rolling Progamme

Date

						Α	ppendix	C.5
Nov						Dec		
Tree						Dee		
d Light	ings							
		Depoiring	~				ter milling of te	
		Repairing		exig conc	ue	ck sunace an	ter mining of te	mp as
	1 1 1 1							
	1 1 1 1							
tion	- 							
						Ohad	A	!
DW	R /P-08 (2) -	evision 3 Months	F	Rolling	T	Checked L	Approv TL	ea
•				-				

Data Date: 20-/	Aug-18	TASK					nissioni Original Se			ry, Not HL.				
ctivity ID	Activity Name		Original Duration	Start	Finish	Total Float				2018	1			
Update 2018	3-08-20 CWB(CC) - Commissio	oning Contract (DWP 4)						Aug		Sep		Oct		Nov
	ARIES AND GENERAL REQUI													
	y Dates and Milestones													
Contract K	ey Dates													
KD002	KD2 - Achievement of Stage 2 (1635 day	s) - include EOT No.12 (403 days)	0		20-Aug-18*	0			â					
KD004	KD4 - Achievement of Stage 4 (1711 days	s) - include EOT No.12 (415 days)	0		04-Nov-18*	-49							2	
KD005	KD5 - Achievement of Stage 5 (1711 day	s) - include EOT No.12 (415 days)	0		04-Nov-18*	-49							2	
KD006	KD6 - Completion of Section 1 of the Wo (415 days)	orks (1711 days) - include EOT No12	0		04-Nov-18*	-49							2	
Anticipated	d Completion Dates													
KD02	KD2 - Achievement of Stage 2 (1635 day	s) - include EOT No.12 (403 days)	0		17-Aug-18 A			•						
KD04	KD4 - Achievement of Stage 4 (1711 days	s) - include EOT No.12 (415 days)	0		31-Aug-18*	16			•					
KD05	KD5 - Achievement of Stage 5 (1711 days	s) - include EOT No.12 (415 days)	0		13-Oct-18*	-27				Δ	٠			
KD11	KD11 - Completion of Section 6 of the We No.12 (149 days)	orks (1445 days) - include EOT	0		13-Oct-18*	-244				▲	٠			
KD06	KD6 - Completion of Section 1 of the Wo (415 days)	orks (1711 days) - include EOT No12	0		18-Oct-18*	-32				▲		•		
Possession	n Dates and Vacation Dates													
PO-IIa	Possession of Portion IIa (Day 1) - WVB	below +6.5mPD	1329	28-Feb-14 A	17-Sep-18	-263								
PO-III	Possession of Portion III (Day 120) - CH1	1805-2600	1209	28-Jun-14 A	17-Sep-18	-267								
PO-lb	Possession of Portion Ib (Day 242) - CH1	1580-1805	1087	28-Oct-14 A	17-Sep-18	-251								
PO-IXd	Possession of Portion IXd (Day 266) - Ch	H4600-4860	1063	21-Nov-14 A	17-Sep-18	-267								
PO-XI	Possession of Portion XI (Day 296) - EVS	5	1033	21-Dec-14 A	17-Sep-18	-1								
PO-IIc	Possession of Portion IIc (Day 336) - CH	1360-1580	993	30-Jan-15 A	17-Sep-18	-263							1	
PO-IIb	Possession of Portion IIb (Day 336) - WV	/B above +6.5mPD	669	30-Jan-15 A	17-Sep-18	-263								
PO-IXa	Possession of Portion IXa (Day 392) - Ch	H4860-5150	937	27-Mar-15 A	17-Sep-18	-267								
PO-Va	Possession of Portion V (Day 607) - CH2	2950-3210	722	28-Oct-15A	17-Sep-18	-249								
			-	ramme	e Upda	nte 54	ร (Asia) I t (Augus ROLLIN	st 2018		Project ID: H2613-U054 Baseline: DWP4 Layout: Update Three Month I U054 Page 1 of 27	Rolling	Date Rev 20-Jul-18 U053 20-Aug-18 U054	AT	cked Approv CW CW

Data Date: 20-A	ug-18	TASK		CWB((-		ot HL.						
ctivity ID	Activity Name		Original Duration	Start	Finish	Total Float						2018	l				
				00 D 45 A	17.0 10				Aug		Sep	2010		Oct			Nov
PO-VII_a1	Possession of Portion VII (Day 762) - CH	(3911-4250 (below -6.0mPD)	659	30-Dec-15 A	17-Sep-18	-263											
PO-Vc	Possession of Portion V (Day 607) - CH3	210-3250	658	15-Jan-16 A	17-Sep-18	-241											
PO-Vlb_b1	Possession of Portion VIb (Day 761) - Ch	H3428-3625 (E/B)	619	18-Feb-16 A	17-Sep-18	-263											
PO-Vlb_b2	Possession of Portion VIb (Day 761) - Ch	H3428-3625 (W/B)	568	29-Feb-16 A	17-Sep-18	-226											
PO-Xa_1	Possession of Portion Xa (Day 650) - AD ref: 2015007890T)	B Southern Portion (AECOM letter	589	07-Mar-16 A	17-Sep-18	-433											
PO-Xb_1	Possession of Portion Xb (Day 804) - AD	B Northern Portion	589	07-Mar-16 A	17-Sep-18	-433											
PO-Vb1	Possession of Portion V (Day 607) - SR3	i	587	11-Mar-16 A	17-Sep-18	-1											
PO-la	Possession of Portion Ia (Day 789) - SCE Flyover	3 / SCP1 / SCP2 / Rumsey Street	600	28-Mar-16 A	17-Sep-18	-416											
PO-VII_a2	Possession of Portion VII (Day 762) - CH	3800-3911 (below -6.0mPD)	567	31-Mar-16 A	17-Sep-18	-263											
PO-IXc_1	Possession of Portion IXc (Day 712) - EV 12 Apr 2016	/B above 3.6mPD - Relinguished on	445	29-Jul-16 A	17-Sep-18	-409											
PO-IXb_1	Possession of Portion IXb (Day 712) - EV slab) - Relinguished on 12 Apr 2016	/B (below +3.6mPD to tunnel top	445	05-Aug-16 A	17-Sep-18	-409											
PO-VIa_a	Possession of Portion VIa (Day 823) - CH	-3250-3283	425	15-Aug-16 A	17-Sep-18	-226											
PO-Vb2_a	Possession of Portion V (Day 607) - SR2		456	15-Aug-16 A	17-Sep-18	-266											
PO-VIc_a	Possession of Portion VIc (Day 761) - CH	13770-3800 (Access Shaft Opening)	391	23-Sep-16 A	17-Sep-18	-263											
PO-Vlb_c	Possession of Portion VIb (Day 761) - CH	-13625-3770	391	23-Sep-16 A	17-Sep-18	-263											
PO-IVa1	Possession of Portion IVa (Day 930) - CH	12600-2720	323	30-Nov-16 A	17-Sep-18	-249											
PO-IVb2	Possession of Portion IVb (Day 930) - MV	/B (GLD-H)	233	28-Feb-17 A	17-Sep-18	-457											
PO-VIIIa_a	Possession of Portion VIIIa (Day 929) - C	CH4530-4591 W/B	233	28-Feb-17 A	17-Sep-18	-267											
PO-VIIIa	Possession of Portion VIIIa (Day 929) - C	CH4250-4600 (Remaining)	241	12-Mar-17 A	17-Sep-18	-267											
PO-VIIIb	Possession of Portion VIIIb (Day 929) - S	R8 (CH700-350)	233	12-Mar-17 A	17-Sep-18	-249											
PO-VIIIc	Possession of Portion VIIIc (Day 1039) -	SR8 (CH350-310) / SCP4	233	12-Mar-17 A	17-Sep-18	-236											
PO-IVa2_a	Possession of Portion IVa (Day 930) - CH	12720-2950	241	12-Mar-17 A	17-Sep-18	-249											
PO-IVb1	Possession of Portion IVb (Day 930) - MV	/B (GLA-C)	239	14-Mar-17 A	17-Sep-18	-457											
PO-IVa2_b	Possession of Portion IVa (Day 930) - SF	1	203	30-Mar-17 A	17-Sep-18	-249											
Leve			-	hton C ramme THRE		ate 54	l (Au	gust	2018)	Base Layo U05	ect ID: H2613 eline: DWP4 out: Update T 4 e 2 of 27		Rolling	Date 20-Jul-18 20-Aug-18	Revisic U053 U054	n Chei AT AT	Cked Approv CW CW

Data Date: 20-A	ug-18	TASK		CWB(HL.						
ctivity ID	Activity Name	I	Original Duration	Start	Finish	Total Float					2	018					
PO-Vb2_b	Possession of Portion V (Day 607) - SCF	23	182	03-Jul-17A	17-Sep-18	-266	:		Aug		Sep			Oct			Nov
PO-VIb_a	Possession of Portion VIb (Day 761) - C	H3400-3428	80	31-Jul-17 A	17-Sep-18	-226			-								
PO-Vla_b	Possession of Portion VIa (Day 823) - C	H3283-3400	80	31-Jul-17A	17-Sep-18	-249				 							
PO-IVc	Possession of Portion IVc (Day 1144) - N	/VB (above +5.0mPD)	111	20-Aug-18	08-Dec-18	-268											
Submission	ns and Approvals	. ,		-													
	ral Submission																
10168	Submission of CMC 3DVR		30	20-Aug-18	18-Sep-18	-2											
	DESIGN OF WORKS			20 / 10	10 000 10					 							
	Works Design and Engineerin	ng															
Green Wall																	
10238	ADB Green Wall - Engineer review & Ap Constructiion	· · ·	24	07-Mar-16 A	25-Aug-18	-376											
Landscapin	g & Associated Irrigation Systen	ו															
10268	Landscaping - Engineer review & Approv Constructiion	al; Consent to Proceed	24	07-Mar-16 A	01-Sep-18	-357											
PROCUREN	MENT, MANUFACTURING & I	DELIVERIES															
Procuremen	nt; Manufacturing; Deliveries																
Landscapin	g and Associated Irrigation Syst	em															
Shop Drawi	ngs																
10272	Landscaping - Shop Drawings submissio	n to the Engineer	30	06-Oct-17 A	31-Aug-18	-469											
12848	Landscaping - Shop Drawings review by	the Engineer	30	01-Sep-18	30-Sep-18	-469											
10274	Landscaping - Obtain Approval for Shop	Drawings	0		30-Sep-18	-469							•				
Procuremen	nt & Fabrication		·														
10276	Landscaping - Confirm design of embed	items	0	01-Oct-18		-469							•				
10278	Landscaping - Embed fabrication & delive	ery	12	01-Oct-18	12-Oct-18	-469							-	•			
10280	Landscaping - Commence embed install	ation	0	13-Oct-18		-469								•			
Leve		ojou Buosii io	-	hton C ramme THRE		ate 54	• (A)	ugust	2018)	Baseli Layou U054	t ID: H2613-I ne: DWP4 t: Update Th 3 of 27		Rolling	Date 20-Jul-18 20-Aug-18	Revision U053 U054	on Che AT AT	cked Approv CW CW

Data Date: 20-	Aug-18	TASK		CWB(y, Not I	4L.						
Activity ID	Activity Name		Original Duration	Start	Finish	Total Float					-	2	2018	I				
10282	Landscaping - Fabrication & delivery		18	13-Oct-18	30-Oct-18	-469			Aug			Sep			Oct	_		Nov
10284	Landscaping - Commence installation		0	31-Oct-18		-469										•		
Green Wa	II on ADB																	
Shop Drav																		
	ADB Green Wall - Shop Drawings review	utha Engine ar	10	11 Apr 10 A	0E Aug 10	405												
12850			18	11-Apr-18 A	25-Aug-18	-465												
10244	ADB Green Wall - Obtain Approval for S	hop Drawings	0		25-Aug-18	-465												
Procurem	ent & Fabrication																	
10246	ADB Green Wall - Confirm design of em	bed items	0	26-Aug-18		-465				•								
10248	ADB Green Wall - Embed fabrication & c	blivery	30	26-Aug-18	24-Sep-18	-465	-4											
10250	ADB Green Wall - Commence embed in	stallation	0	25-Sep-18		-465							•					
10252	ADB Green Wall - Green Wall Fabrication	n & delivery	52	25-Sep-18	15-Nov-18	-465									_			-
10254	ADB Green Wall - Commence installation	1	0	16-Nov-18		-465			۵									•
Architechu	Iral Feature on EVS																	
Procurem	ent & Fabrication																	
10086	EVS - Architechural Features delivery		60	02-Jun-17 A	29-Aug-18	-224												
CONSTRU	ICTION																	
West Vent	ilation Building (WVB - related)																	
West Ven	tilation Building (WVB)																	
External V	Vorks																	
3104	WVB - External Fence Wall (VO/131 - F	ence wall and metal gate revision)	48	28-Aug-17 A	08-Aug-18 A													
3106	WVB - Final completion works (include C	CMS interface)	48	23-May-18 A	01-Sep-18	-160												
10884	WVB - External lamp pole, bollard & rece	ess wall lighting installation	48	23-May-18 A	25-Aug-18	-154												
E&M Testi	ng &Commissioning / Statutory Ins	pection																
3120a4	MEP(WVB) - TVS N-mode Test (Stage)	54	23-Jun-18 A	01-Aug-18 A													
					-													
			ate 54	(Au	gust	mited 2018)		Baselin	ID: H2613- e: DWP4 Update Th		Rolling	Date 20-Jul-1 20-Aug		sion Cheo AT AT	ked Approv CW CW			
	tical Remaining Work			IHRE	E MO	NIH	KOL	LING	Í		Page 4	of 27						

Data Date: 20-A	\ug-18	TASK	filters	CWB(s: 3 Montl					-	-			t HL.						
ctivity ID	Activity Name	I	Original Duration	Start	Finish	Total Float						-		2018	1				
3120d	MEP(WVB) - LUX measurement for tun	nel lighting	23	20-Aug-18	11-Sep-18	-249				Aug			Sep			Oct			Nov
Final Comp	pletion Works																		
3132	WVB - APS Site Acceptance Test (Air mo	pnitoring station)	42	17-Mar-18 A	25-Aug-18	-39													
191501a	WVB - LHDS extra controllers deliver to	site	0		08-Aug-18 A				٠										
191503a	WVB - LHDS extra controller (Changed installation	from Non-FSI to FSI item) -	6	09-Aug-18 A	17-Aug-18 A														
191505a	WVB - LHDS extra controller(Changed f	rom Non-FSI to FSI item) - T&C	9	18-Aug-18 A	21-Aug-18	- 198				1	-								
3134	WVB - TCSS & other E&M systems Site	Acceptance Test	18	20-Aug-18	06-Sep-18	-251		-											
KD04M2	APS SAT (WVB) - Milestone for KD04		0		25-Aug-18	22					•								
3140	WVB - Completion of Section 1 (KD06)		0		01-Sep-18	-202		4	▲			٠							
KD05M2	TCSS SAT (WVB) - Milestone for KD05		0		06-Sep-18	10		▲				•							
Landscapi	ng and Irrigation Systems																		
3136	WVB - Final completion test for irrigation	systems in Portion IIb	60	20-Aug-18	18-Oct-18	-457			•										
3138	WVB - Landscape Works in Portion IIb (lightning protection system installation)	Include architectural lightings &	60	31-Oct-18	29-Dec-18	-469											f		
FSD Comm	nent on TVS and SES at WVB (Fire I	Resistance Rating "FRR" Imp	rovemen	t Works)															
NOC-175																			
NOC175_0	2 NOC175 - Material order and delivery to	site	12	07-Jul-18 A	20-Jul-18 A														
NOC175_0	3 NOC175 - Construct additional durastee	l board system at Rm. L2-02	6	21-Jul-18 A	27-Jul-18 A														
NOC175_0	4 NOC175 - Replace higher F.R.R. (-/240)	/240) door at L2-01A & L2-04A	6	28-Jul-18 A	03-Aug-18 A														
NOC175_0	5 NOC175 - Construct additional solid con	crete wall (MC2) at Rm L2-04	18	04-Aug-18 A	06-Sep-18	-218													
	6 NOC175 - Make good the finishes of the	affected rooms and areas	6	07-Sep-18	13-Sep-18	-218													
	xible Pavement (WVB-related)																		
5802	Road(WB) - (CH1480 to CH2600) Road		14	13-Jun-18A	31-Jul-18 A														
5806	Road(EB) - (CH1480 to CH2600) Road	Marking & Traffic Sign	14	15-Jun-18A	31-Jul-18 A					-									
Satellite Co	ontrol Building (SCB)																		
•		emaining Work	Lein	hton (Contra	ctors	(Δ	sia) ir	nited		-	ect ID: H2613	3-U054		Date	Revis		cked Approv
	el of Effort Pr	ojou busenio	_	ramm			•		•				eline: DWP4 ut: Update T	hree Month	Rolling	20-Jul-18 20-Aug-18	U053 U054	AT AT	CW
Adu	ual Work				EE MO		-	_			,	U054	, t		, coning			ſ	
Critic	cal Remaining Work											Page	e 5 of 27						

Da	ta Date: 20-A	ug-18	TASK						oning Contr I Sections, No Su		/, Not HL.				
ctivit	/ ID	Activity Name		Original Duration	Start	Finish	Total Float				2018				
	Final Comp	letion Works							Aug		Sep		Oct	N	ov
Г	3958	SCB - TCSS & other E&M systems Site A	Acceptance Test	90	10-May-18 A	25-Jul-18 A									
┢	3962	SCB - Completion of Section 1		0		25-Jul-18 A		•							
┠	KD05M6	TCSS SAT (SCB) - Milestone for KD05		0		25-Jul-18 A		•							
	Satellite Co	ntrol Points 1 / 2													
Г	SCP1														
Γ	3720	MEP (SCP1) - E&M Final Completion W	lorks	12	11-Jul-18 A	26-Jul-18 A									
	KD01M2	MEP (SCP1) - Milestone for KD06		0		26-Jul-18 A		•							
	SCP2	I													
Γ	3742	MEP (SCP2) - E&M Individual System T&	šC	12	10-Jul-18 A	26-Jul-18 A									
	3744	MEP (SCP2) - E&M Final Completion W	lorks	12	10-Jul-18 A	26-Jul-18 A									
	KD01M3	MEP (SCP2) - Milestone for KD06		0		26-Jul-18 A		•							
	Middle Vent	ilation Building (MVB - related	1)												
	Tunnel Sed	tion (MVB-related)													
	Portion IVa	(CH2600 to CH2950)													
	Slip Road 1														
	10024	MEP(SR1) - (CH171 to CH271) TCSS F	Field equip & cable installation	6	24-May-18 A	27-Aug-18	2								
	10046	MEP(SR1) - (CH171 to CH271) VE Pan	el installation (Upper part) (1200m2)	13	28-Jun-18 A	22-Aug-18	-182								
	10046d	VO 238 - SR1 - Installation of granite sto		40	09-Jul-18 A	28-Jul-18 A			┿	_					
	10046c	VO 238 - SR1 - Construction of D-wall p		12	10-Jul-18 A	23-Aug-18	-213								
	10024a	MEP(SR1) - (CH171 to CH271) Access		0	20-Aug-18*		3								
	10046e	VO 238 - SR1 - Application of Evonik Pro	otectosil SC60	6	21-Sep-18	28-Sep-18	-213								
		CH2950 to CH3210]													
	Westbound	(Outer Lane)													
	Leve Actu				ramme		ate 54	1 (Au	a) Limited gust 2018) LING		Project ID: H2613-U054 Baseline: DWP4 Layout: Update Three Month R U054 Page 6 of 27	-	Date Rev 20-Jul-18 U053 20-Aug-18 U054	AT	ed Approv CW CW

Data	Date: 20-A	ug-18	TASK	filters	CWB(y, Not∣	HL.						
ctivity ID)	Activity Name		Original Duration	Start	Finish	Total Float		1				2	2018		2			
	9954a	MEP(WB) - (CH2950 to CH3210) VE Pa (1800m2)	nel installation (Upper part)	20	11-Apr-18 A	25-Aug-18	-185			Aug			Sep			Oct			Nov
	Eastbound ((Outer Lane)																	
	9956a	MEP(EB) - (CH2950 to CH3210) VE Par (1800m2)	nel installation (Upper part)	20	09-Apr-18 A	25-Aug-18	-185												
F	Portion Vb1	(SR3)																	
	Slip Road 3																		
	10032b	MEP(SR3) - (CH3089 to CH3334) E&M	1st Fix	13	15-Mar-17 A	23-Aug-18	-183												
	10036b	MEP(SR3) - (CH3089 to CH3334) TCSS	S Field equip & cable installation	8	15-Mar-17 A	23-Aug-18	-183												
	10034b	MEP(SR3) - (CH3089 to CH3334) E&M	2nd Fix (include Sump C)	27	11-Apr-18 A	25-Aug-18	-185												
	10038b	MEP(SR3) - (CH3089 to CH3334) E&M	Final Fix	8	16-Apr-18 A	27-Aug-18	-186												
	10048c2	MEP(SR3) - Road lighting installation (Pe	ortal)	18	12-Jun-18 A	01-Sep-18	-191												
	10048b	MEP(SR3) - (CH3089 to CH3334) VE Pa (2940m2)	anel installation (Upper part)	33	04-Jul-18A	27-Aug-18	-186												
	10048g	VO 238 - Installation of granite stone		5	11-Jul-18A	30-Jul-18 A													
	10048h	VO 238 - Installation of precast concrete		22	24-Jul-18 A	11-Sep-18	-206												
	10048i	VO 238 - Application of Evonik Protectosi	ISC60 at SR3	7	12-Sep-18	19-Sep-18	-206												
F	Portion Vb2	(SR2 / SCP3)																	
	Slip Road 2																		
	10050b	MEP(SR2) - (CH3114 to CH3257) E&M	1st Fix	8	08-Mar-17 A	21-Aug-18	-181												
	10056b	MEP(SR2) - (CH3114 to CH3257) TCSS	Field equip & cable installation	5	16-Mar-17 A	23-Aug-18	-183				-								
	10052b	MEP(SR2) - (CH3114 to CH3257) E&M	2nd Fix (include Sump F)	40	15-Jun-17 A	25-Aug-18	-185												
	10054b	MEP(SR2) -(CH3114 to CH3257) E&M F	Final Fix	5	08-May-18 A	25-Aug-18	-185												
	10064b2	MEP(SR2) - Road lighting installation (Pc	ortal)	18	12-Jun-18 A	01-Sep-18	-191												
	10064b	MEP(SR2) - (CH3114 to CH3257) VE Pa (1716m2)	anel installation (Upper part)	18	09-Jul-18 A	25-Aug-18	-185												
	-	CH3210 to CH3250]																	
	Westbound	(Outer Lane)																	
_	-		maining Work	Leid	hton C	ontra	ctors	(Asia	a) Lim	ited			ID: H2613-	U054		Date	Revis		cked Approv
▲		el of Effort Pro		-	ramme			-	-				ie: DWP4 : Update Th	ree Month	Rollina	20-Jul-18 20-Aug-1	_	AT AT	CW CW
_ -	_	al Work	'	9		EE MO			-			U054				ļ	_!	I	
-	- Critic	al Remaining Work										Page 7	of 27						

Data Date: 2	20-Aug-18	TASK	filters				nissioning Contrac Original Sections, No Sum			
ctivity ID	Activity Name	I	Original Duration	Start	Finish	Total Float		2018	1	
9954c	MEP(WB) - (CH3210 to CH3250) VE Pa	anel installation (Upper part)	20	10-Jul-18A	30-Aug-18	-189	Aug	Sep	Oct	Nov
Eastbo	(1800m2) und (Outer Lane)									
9956c	MEP(EB) - (CH3210 to CH3250) VE Pa (1800m2)	nel installation (Upper part)	20	06-Jul-18 A	25-Aug-18	-185				
Portion	Vla [CH3250 to CH3283]									
Westbo	und									
9958a	MEP(WB) - (CH3250 to CH3283) VE Pa (528m2)	anel installation (Upper part)	6	19-Apr-18 A	21-Aug-18	-181				
Eastbou	Ind									
9960a	MEP(EB) - (CH3250 to CH3283) VE Pa	nel installation (Upper part) (528m2)	6	18-Apr-18 A	21-Aug-18	-181				
Portion	Vla [CH3283 to CH3400]									
Westbo	und									
9958b	MEP(WB) - (CH3283 to CH3400) VE Pa (1872m2)	anel installation (Upper part)	21	10-Apr-18A	25-Aug-18	-185				
Eastbou	Ind									
9960b	MEP(EB) - (CH3283 to CH3400) VE Pa (1872m2)	nel installation (Upper part)	21	16-Apr-18 A	25-Aug-18	-185				
Middle	/entilation Building (MVB)									
Externa	I Facade									
3238	MVB - External facing tiles / Louvre		90	06-Nov-17 A	14-Aug-18 A					
MEP Wo	orks									
3236	MVB - Metal works / steel platform / Lad	ders / Handrails	48	06-Dec-17 A	10-Aug-18 A					
3248	MEP(MVB) - TCSS Enabling Works (Re	maining TCSS installation)	24	03-Jan-18 A	23-Jul-18 A		→			
3252	MEP(MVB) - E&M Final Completion Wor	rks; Ready for Statutory Inspections	24	31-May-18 A	16-Aug-18 A					
3280a10	Rectification works for lift shaft structure	by lift contractor / WDII / C3	6	03-Aug-18 A	09-Aug-18 A					
E&M Inc	lividual System T&C									
3250c	MEP(MVB) - Lift functional test		12	06-Jul-18 A	09-Aug-18 A					
Baseme	ent 2 (GL D - H)									
•	Current Milestone	emaining Work		uhton () ontro	otora	(Acia) Limitad	Project ID: H2613-U054	Date	Revision Checked Approv
							(Asia) Limited	Baseline: DWP4		053 AT CW
	Baseline Milestone Actual Work	H	rog				(August 2018)	Layout: Update Three Month Rolli	ng 20-Aug-18 U	054 AT CW
	Critical Remaining Work			THRE	EE MO	NTH	ROLLING	U054 Page 8 of 27		

Da	ta Date: 20-A	.ug-18	TASK						oning Contr al Sections, No Su		, Not I	HL.						
ctivit	/ ID	Activity Name		Original Duration	Start	Finish	Total Float	_		-)18	•				
	Basement	t 2 - Other Rooms / General Area & 0						1 1	Aug		1	Sep			Oct			Nov
				40	40 E-h 40 A	05 14 40 4												
	19034	MEP(MVB) - E&M final fixing		18	12-Feb-18 A	25-Jul-18 A												
	Basement 2	2M (GL D - H)																
	Basement	t 2M - Other Rooms / General Area 8	k Corridor															
	19051	MEP(MVB) - E&M final fixing		18	07-Mar-18 A	03-Aug-18 A												
	Basement 1	(GL D - H)																
	Other Roo	oms / General Area & Corridor																
	11318	MEP(MVB) - E&M final fixing		24	20-Feb-18 A	15-Aug-18 A												
					201001071	ie nag iert												
	Basement 1																	
	MCC Roon	n 1 (B1-04)																
	11286	MEP(MVB) - E&M final fixing		24	25-Nov-17 A	14-Aug-18 A												
	G/F (GL D -	H)																
	TVF Fan R	oom 2 (G-02)																
	11404	MEP(MVB) - E&M final fixing		24	03-Mar-18 A	25-Jul-18 A												
	Other Roo	oms / General Area & Corridor																
	11412	MEP(MVB) - E&M final fixing		24	21-Feb-18 A	07-Aug-18 A												
						or rug fort												
	G/F (GL A -																	
	Fire Contro	ol Centre (G-11)																
	11380	MEP(MVB) - E&M final fixing		12	02-Mar-18 A	26-Jul-18 A												
	Other Roo	oms / General Area & Corridor																
	11388	MEP(MVB) - E&M final fixing		24	02-Mar-18 A	02-Aug-18 A			┿ ! ! !									
	1/F (GL D -	H)																
	Other Roo	oms / General Area & Corridor																
	11446	MEP(MVB) - E&M final fixing		18	21-Feb-18 A	16-Aug-18 A												
		()																
	🔶 Curr	rent Milestone	emaining Work	pin	hton (ontra	ctore	s (Aei	a) Limited		Project	ID: H2613-L	J054		Date	Revis		ked Approv
			ojou Buoomio	_				-	-			e: DWP4			20-Jul-18 20-Aug-18		AT	CW
		eline Milestone Ial Work		rug					gust 2018)		Layout: U054	Update Thr	ee Month	Rolling	20-AUG-18	0054	AT	CW
		al Remaining Work			IHRE	EE MO	NIH	ROL	LING		Page 9	of 27						
											-							

Dat	a Date: 20-A	\ug-18	TASK		CWB(3 Month						•				ot HL.									
ctivity	ID	Activity Name		Original Duration	Start	Finish	Total Float	at								2018	}							
	1/F (GLA -	D)						1				Aug			S	ер	:		Oct			i	Nov	1
		Tank & Pump Room (L1-05)																						
	11420	MEP(MVB) - E&M final fixing		12	15-Mar-18 A	24-Jul-18 A																		
	Other Roo	oms / General Area & Corridor																						
	11438	MEP(MVB) - E&M final fixing		18	15-Feb-18 A	09-Aug-18 A																		
1	Smoke Extr	raction System (B3/F - G/F)																						
	B3/F - G/F																							
	191485	SES(MVB) - Termination		6	16-Jun-18 A	23-Jul-18 A																		
	191487	SES(MVB) - Testing & Commissioning		12	24-Jul-18 A	07-Aug-18 A					-													
Ľ	External Wo	orks																						
Г	3258	MVB - External concrete pavement		42	04-Apr-18A	30-Aug-18	-158	8																
	3262	MVB - Final completion works (include C	CMS interface)	30	05-Apr-18 A	30-Aug-18	-158	8																
┣	3260	MVB - External Fence Wall		42	10-Apr-18A	30-Aug-18	-158	8				: : : :												
	E&M Testin	g &Commissioning / Statutory Insp	pection																					
Г	3264	MEP(MVB) - E&M System Integrated Tes	sting and Commissioning	24	23-Jul-18 A	31-Aug-18	-261	1				<u> </u>												
	3264a	MEP(MVB) - TVS & CCMS System Integ	grated Testing and Commissioning	24	23-Jul-18 A	31-Aug-18	-261	1																
	3264b	MEP(MVB) - Tunnel Lighting & CCMS S Commissioning	stem Integrated Testing and	24	23-Jul-18 A	31-Aug-18	-261	1																
	3264c	MEP(MVB) - Fire Services & CCMS Syst Commissioning	em Integrated Testing and	24	23-Jul-18 A	31-Aug-18	-261	1																
	3264a4	MEP(MVB) - TVS N-mode Test (Stage 2)	54	10-Aug-18 A	31-Aug-18	-238	8																
	12606	MEP(MVB) - Submission of Form 5 to Ef	MSD	0	15-Aug-18 A							٠												
	3266	MEP(MVB) - Ready for Statutory Inspect	ion	0	17-Aug-18 A							•												
	12622b	MEP(MVB) - Submission of Form 501 to	FSD (include SES / SPS) (Building)	0	17-Aug-18 A							•												
	12650	MEP(MVB) - Submission of Form 314 to	FSD	0	17-Aug-18 A							•												
	KD02M1	MEP(MVB) - Milestone for KD02		0		17-Aug-18 A						•												
	🔶 Curr	rent Milestone	maining Work		hton () o o tro		_ /	<u>ا</u>		1	it a d	+	Pro	ject ID: H	2613-110	54			Date	Revisi	on Cł	ecked	Approv
			oject Baseline	-	hton C			-	•	-					seline: DV		~ '				U053	A		CW
<u> </u>		eline Milestone	F	rog	ramme	-			-	-		018)			out: Upda	ate Three	Month I	Rolling	20-	Aug-18	U054	A	-	CW
		ual Work xal Remaining Work			THRE	EE MO	NTH	I R	lOI	LLII	NG			U0	54 je 10 of 2	7								
														Paç	10 01 2	1								

Data Date: 20)-Aug-18	TASK					nissioning Cont Original Sections, No S		y, Not HL.			
Activity ID	Activity Name	I	Original Duration	Start	Finish	Total Float			2018	1		
12638	MEP(MVB) - Submission of WWO46 (Pr	art IV) to WSD	0	20-Aug-18		-281	Aug		Sep	Oct	Nov	
3264d	MEP(MVB) - LUX measurement for tunn	nel lighting	24	27-Aug-18	19-Sep-18	-281						
3268	MEP(MVB) - Statutory Inspection & Cert	ificates (include EMSD & FSD	8	29-Aug-18	06-Sep-18	-212		_				
12606a	inspection) (Building) MEP(MVB) - Use Permit - Lift		0	29-Aug-18		-267		•				
12640	MEP(MVB) - Submission of WWO46 (Pa	art V) to Client	0	10-Sep-18		-270	▲		•			
Final Co	mpletion Works											
191491	MVB - LHDS (Changed from Non-FSI to	FSI item) - installation	24	14-May-18 A	18-Aug-18 A							
3272	MVB - APS Site Acceptance Testing (Air	monitoring station)	30	13-Jun-18A	31-Aug-18	-45						
3270	MVB - Final Completion works for APS (Charcoal installation)	30	14-Jul-18A	09-Aug-18 A							
191489a	EVB - LHDS extra controllers deliver to s	ite	0		08-Aug-18 A		•					
191493	MVB - LHDS (Changed from Non-FSI to	o FSI item) - T&C	9	19-Aug-18 A	24-Aug-18	-201						
3288	MVB - Completion of Section 1 (KD06)		0		20-Aug-18	-189						
KD04M3	APS SAT (MVB) - Milestone for KD04		0		31-Aug-18	16		•				
192030	VO 434 - Provision of Protective Cover fe	or Utilities	6	07-Sep-18	12-Sep-18	-2						
192032	VO 426 - Seal water seepage on ceiling/ (MVB B3-04)	Remove and re-install trunking	6	07-Sep-18	12-Sep-18	-2						
192034	VO 426 - Construct U-channel/drain pipe D-wall to Sump Pump at MVB B3-13	e tp collect seepage water from	6	13-Sep-18	18-Sep-18	-2						
192036	VO 442 -Seal water seepage at MVB ST floor slab & remove and reinstate floor so		6	13-Sep-18	18-Sep-18	-2						
3274	MVB - TCSS & other E&M systems Site	Acceptance Test	18	19-Sep-18	06-Oct-18	-20						
KD05M3	TCSS SAT (MVB) - Milestone for KD05		0		06-Oct-18	-20	Δ			•		
Landsca	ping and Irrigation System											
3276	MVB - Final completion test for irrigation	systems in Portion IVa and IVb	60	20-Aug-18	18-Oct-18	-457	-					
3278	MVB - Landscape Works in Portion IVa a	and IVb	60	31-Oct-18	29-Dec-18	-469						
Tunnel F	lexible Pavement (MVB-related)											
5810	Road(WB) - (CH2600 to CH3770) Road	d Marking & Traffic Sign	12	05-Jul-18 A	09-Aug-18 A			_				
		ojou Dusomio	-	ramme	e Upda	ate 54	(Asia) Limited (August 2018) ROLLING		Project ID: H2613-U054 Baseline: DWP4 Layout: Update Three Month Rolli U054 Page 11 of 27	Date 20-Jul-18 20-Aug-18	U053 AT	d Approv CW CW

Data Date: 20-A	ug-18	TASK		CWB(y, Not HL								
Activity ID	Activity Name		Original Duration	Start	Finish	Total Float	t		,		,	201	8						
5814	Road(EB) - (CH2600 to CH3770) Road	Marking & Traffic Sign	12	09-Jul-18 A	09-Aug-18 A				Au	g		Sep			Oct	:		N	ov
Deutieus IV/e		0 0			Ū						 								
	Road Surface Area																		
191525b	NOC 151 - WDII area - Revised signage	e manufacturing and delivery	48	07-May-18 A	23-Aug-18	-189	9												
191525	WDII area - TCSS equipment / signage / termination	/ lumimeter installation, cabling &	24	16-Jul-18 A	24-Aug-18	-190													
191523b	NOC 180 - AECOM iinstruct CC to do civ 21-Jul-2018)	vil provision by e-mail on	0	21-Jul-18A			•												
191523c	NOC 180 - CC works on civil provisioin		0	21-Jul-18A	21-Aug-18	-189													
191527	WDII area - TCSS SCT		24	16-Aug-18 A	08-Sep-18	-203	3												
Satellite Co	ntrol Point 3																		
SCP3																			
10110	MEP(SCP3) - TCSS Enabling Works (Re	emaining TCSS installation)	12	18-Jul-18 A	31-Jul-18 A			-											
3768	MEP(SCP3) - E&M Individual System T8	kC	12	20-Aug-18	01-Sep-18	-211					 •								
3770	MEP(SCP3) - E&M Final Completion W Inspections	orks; Ready for Statutory	12	03-Sep-18	15-Sep-18	-211						-							
KD02M2	MEP(SCP3) - Milestone for KD06		0		15-Sep-18	0	D					•							
East Ventila	tion Building (EVB - related)					,													
Tunnel Sec	tion (EVB-related)																		
Portion VII	[CH3800 to CH3911]																		
Eastbound											 								
9968a4	MEP(EB) - (CH3800 to CH3911) VE Par (1332m2)	nel installation (Upper part)	14	09-Apr-18 A	21-Aug-18	-210													
Portion VII	[CH3911 to CH4250]																		
Access Sha	ft Opening																		
10120a3	VI(WB) - Backfilling (78 layers; 1 day/lay	ver)	78	05-Apr-18 A	26-Jul-18 A														
Westbound	l										 								
9966a2	MEP(WB) - (CH3911 to CH4250) VE Pa (4068m2)	anel installation (Upper part)	21	11-Apr-18 A	21-Aug-18	-210													
Eastbound					·														
Curr	ent Milestone	emaining Work	1	htor C)	-					 Project ID:	H2613-11		i	Date	Re	evision	Check	ed Approv
-		oject Baseline	-	hton C			•	-			Baseline: [20-Jul-1			AT	CW
	eline Milestone	F	Prog	ramme						B)	Layout: Up	date Thre	e Month F	Rolling	20-Aug-	-18 U05	54	AT	CW
	ial Work xal Remaining Work			THRE	EE MO	NTH	ROL	LINC	3		U054	: 07							
											Page 12 of	21							

Da	ata Date: 20- <i>I</i>	Aug-18	TASK		CWB(s: 3 Month									Not HI									
ctivit	y ID	Activity Name		Original Duration	Start	Finish	Total Float	t								2018	I						
	9968a2	MEP(EB) - (CH3911 to CH4250) VE Par	nel installation (Upper part)	12	14-Apr-18 A	21-Aug-18	-210)	1		A	lug			Sep			Oc	t			Nov	
Ш	Portion VIII	(4086m2) a [CH4250 to CH4600]																					
													 				+						
	Eastbound																						
	9972	MEP(EB) - (CH4250 to CH4600) VE Par (3900m2)	nel installation (Upper part)	11	24-Jan-18 A	21-Aug-18	-210																
	Portion IXd	[CH4600 to CH4860]																					
Γ	Eastbound																						
	9976	MEP(EB) - (CH4600 to CH4860) VE Par (3300m2)	nel installation (Upper part)	37	22-Mar-18 A	21-Aug-18	-210)				-											
ľ	Portion IXa	[CH4860 to CH5150]											 										
	Eastbound																						
	5346	MEP(EB) - (CH4860 to CH5150) E&M F	Final Fix	10	14-Mar-18 A	27-Jul-18 A			-														
	9980	MEP(EB) - (CH4860 to CH5150) VE Par (3288m2)	nel installation (Upper part)	37	05-Apr-18 A	23-Aug-18	-212																
	East Ventila	ation Building (EVB)																					
Γ	RC Structu	res and Green Roof																					
	3456	EVB - Green Roof (include architectural installation)	lighting & lightning protection system	42	19-May-18 A	01-Sep-18	-330																
	External Fa	acade																					
Γ	3438	EVB - External facing tiles / Treated Was	ste Wood / Louvre	90	11-Sep-17 A	22-Sep-18	-298	3								-							
ŀ	192020	VO/335 - Material submission for approv	al	6	20-Aug-18	25-Aug-18	-30																
	191613	VO/335 - Manufacture and delivery of sn	noke vent cover	24	27-Aug-18	22-Sep-18	-30)					 										
	191615	VO/335 - smoke vent cover installation and	nd cable termination	18	24-Sep-18	16-Oct-18	-30									_		_					
	191617	VO/335 - smoke vent cover T&C (Assum further confirmation from AECOM / FSD)		6	18-Oct-18	24-Oct-18	-30)															
	MEP Work	s																					
ſ	3452	MEP(EVB) - E&M Final Completion Wor	ks; Ready for Statutory Inspections	21	11-Apr-18 A	01-Sep-18	-220)							-								
	E&M Indivi	dual System T&C											 										
	3660d	MEP(ADB) - LUX measurement for tunn	nel lighting	28	20-Aug-18	16-Sep-18	-254	ŀ				-											
	Lev		ojou Duocii ic	-	hton C ramme THRI		ate 54	4 (<i>I</i>	Aug	gus	t 201		 E L	Project ID Baseline: ayout: Uj J054 Page 13 c	DWP4 odate Th	U054 ree Mont	h Rolling		Date D-Jul-18 D-Aug-18	Revisi U053 U054	on Ch AT AT	ecked Ap CV CV	N

D	ata Date: 20-A	ug-18	TASK		CWB(ry, Not HL.						
ctiv	ty ID	Activity Name		Original Duration	Start	Finish	Total Float					-	2018					
	External Wo			Balation				;	; ;	Aug		Se		; ;	Oct	;	1	Nov
	3462	EVB - Final completion works (include CO	CMS interface)	30	17-Jan-18 A	31-Aug-18	-219											
	192026	VO/322 - Preparation works and trimmin	g to formation level	42	20-Jun-18 A	24-Aug-18	13											
	192028	VO/322 - Hard pavement laying		6	25-Aug-18	31-Aug-18	13											
	E&M Testin	g &Commissioning / Statutory Insp	pection															
	3464	MEP(EVB) - E&M System Integrated Tes	ting and Commissioning	36	28-Mar-18 A	31-Aug-18	-275											
	3468	MEP(EVB) - Statutory Inspection & Certil inspection) (Building)	ficates (include EMSD & FSD	7	14-Jul-18 A	30-Jul-18 A												
	12634	MEP(EVB) - Submission of WWO46 (Pa	rt IV) to WSD	0	20-Aug-18		-317											
	12636	MEP(EVB) - Submission of WWO46 (Pa	rt V) to Client	0	10-Sep-18		-270					•						
	Zitron Fan I	High Temperature Test																
	191577	Issue test reports to FSD and get Fire Te	st Certificate	12	29-Sep-18	13-Oct-18	-225											
	191579	Fire Test Certificate received		0		13-Oct-18	-225											
	Fan - 517	.5kW																
	191547	Return the motor to factory and carry Hig	gh Termperature Test	12	19-Jul-18 A	03-Aug-18 A												
	191549	Complete the test and issue test report		12	04-Aug-18 A	21-Aug-18	-193				•							
	Reinstate	Fan - 517.5kW																
	191545	517.5kW - Fabricate new motor and shi	p to Zitron	92	19-Jun-18 A	06-Oct-18	-58											
	191551	517.5kW - Fan installation and route tes	ting by Zitron	6	08-Oct-18	13-Oct-18	-58											
	191589	517.5kW - Deliver to site		24	15-Oct-18	12-Nov-18	-58											
	191557	517.5kW - Install the new fan and recon	nect all power and control cables	6	13-Nov-18	19-Nov-18	-58											
	Fan - 253k																	
	191561	WEG fabricate new 253kW motor and se	end to Zitron	56	19-Jun-18 A	23-Aug-18	-206				-							
	191567	Assemble fan with new motor		1	24-Aug-18	24-Aug-18	-206				I							
	191563	Carry High Termperature Test		4	25-Aug-18	29-Aug-18	-206											
		ent Milestone	maining Work			_					*	Droject ID: 110	612 11054		Date	Revisio	on Che	cked Approv
			oject Baseline	-	hton C			-	-			Project ID: H2 Baseline: DW				U053	AT	CW
Δ	🛆 Base	eline Milestone	P	rog	ramme	e Upda	ite 54	I (A	ugust	2018)		Layout: Updat		th Rolling	20-Aug-18		AT	CW
		al Work al Remaining Work		5		E MO		•	•	-		U054 Page 14 of 27		J				
	—																	

Data	a Date: 20-A	\ug-18	TASK		CWB(3 Month								/, Not HI								
ctivity	ID	Activity Name		Original Duration	Start	Finish	Total Float							20	8	1					
	191565	Complete the test and issue test report		6	30-Aug-18	05-Sep-18	-206	-	: :	Aug	1		-	Sep			Oct			Nov	
	Fan - 212				-																
Ш.																					
	191569	WEG fabricate new 212kW motor and se	end to Zitron	56	19-Jun-18 A	23-Aug-18	-206														
	191575	Assemble fan with new motor		1	24-Aug-18	24-Aug-18	-206				1										
	191571	Carry High Termperature Test		4	25-Aug-18	29-Aug-18	-206														
	191573	Complete the test and issue test report		6	30-Aug-18	05-Sep-18	-206					-									
	Fan - 152																				
	191581	WEG fabricate new 152kW motor and se	end to Zitron	56	19-Jun-18 A	14-Sep-18	-225	-				_									
	191587	Assemble fan with new motor		1	15-Sep-18	15-Sep-18	-225														
	191583	Carry High Termperature Test		4	17-Sep-18	20-Sep-18	-225														
	191585	Complete the test and issue test report		6	21-Sep-18	28-Sep-18	-225							•							
	Final Comp	bletion Works																			
	3472	EVB - APS Site Acceptance Testing (Air n	nonitoring station)	30	17-Mar-18 A	31-Aug-18	-45														
	191497	EVB - LHDS (Changed from Non-FSI to	FSI item) - installation	20	14-May-18 A	14-Aug-18 A															
	191495a	EVB - LHDS extra controllers deliver to s	ite	0		08-Aug-18 A				•											
	191499	EVB - LHDS (Changed from Non-FSI to	FSI item) - T&C	9	15-Aug-18 A	17-Aug-18 A															
	3488	EVB - Completion of Section 1 (KD06)		0		20-Aug-18	-189				>										
	KD04M4	APS SAT (EVB) - Milestone for KD04		0		31-Aug-18	16					•									
	3474	EVB - TCSS & other E&M systems Site A	cceptance Test	18	01-Sep-18	18-Sep-18	-20														
	KD05M4	TCSS SAT (EVB) - Milestone for KD05		0		18-Sep-18	-2							•							
	Landscapi	ng and Irrigation System																			
Г	191539b	VO 311 - Design information from AECO	M (Tentative date)	0	20-Aug-18*		-457				>										
	191539c	VO 311 - Form 542 submission and appr	roval	48	20-Aug-18	06-Oct-18	-457														
	191539d	VO 311 - Excavation & Installation of pipe	es and water points	36	07-Oct-18	11-Nov-18	-457													•	
	Lev				hton C ramme THRE		ate 54	+ (Α ι	igust	2018			Project ID Baseline: Layout: U U054 Page 15 c	DWP4 pdate Thre		olling	Date 20-Jul-18 20-Aug-18	Revisio U053 U054	on Che AT AT	cked Ap CW CW	/

Data Date: 20-A	.ug-18	TASK	filters				nissioning Contract Driginal Sections, No Summary, Not HL.	
ctivity ID	Activity Name		Original Duration	Start	Finish	Total Float	2018	
191539e	VO 311 - WW 046 Part I / II submission a	and cert	36	07-Oct-18	11-Nov-18	-457	Aug Sep	Oct Nov
3476	EVB - Final completion test for irrigation	systems in Portion IXc	52	25-Oct-18	15-Dec-18	-461		
3478	EVB - Landscape Works in Portion IXc		52	31-Oct-18	21-Dec-18	-461		
191539f	VO 311 - WW 046 Part IV submission ar	nd cert	12	12-Nov-18	23-Nov-18	-457		
191539g	VO 311 - Backfill		12	12-Nov-18	23-Nov-18	-457		│
Tunnel Flex	xible Pavement (EVB-related)							
5822	Road(EB) - (CH3770 to CH5149.3) Roa	d Marking & Traffic Sign	12	22-Jun-18 A	10-Aug-18 A			
5818	Road(WB) - (CH3770 to CH5149.3) Road	ad Marking & Traffic Sign	17	26-Jun-18 A	01-Sep-18	-201		
5826	Road(SR8) - (CH210 to CH1000) Road	Marking & Traffic Sign	10	03-Sep-18	13-Sep-18	-201		
Administrat	ion Building (ADB)							
	res (Portion Xa / Xb)							
13484	ADB - Green Wal		35	16-Nov-18	28-Dec-18	-376		
External Fa	cade							
13248	ADB - External facing tiles / Louvre		48	27-Dec-17 A	30-Aug-18	-309		
MEP & ABW			-10	21 200 11 11	oo nag to	000		
13254	MEP(ADB) - TCSS Enabling Works (Rer		30	12-Dec-17 A	25-Aug-18	-335		
13252	ADB - Metal works / steel platform / Lado	lers / Handrails	42	13-Feb-18 A	25-Aug-18	18		
13258	MEP(ADB) - E&M Final Completion Wor	ks; Ready for Statutory Inspections	30	27-Aug-18	02-Oct-18	-335		
External Wo	orks							
13432	ADB - Road and drainage works (EVA)		42	11-Dec-17 A	01-Sep-18	-45		
13438	ADB - Final completion works (include C	CMS interface)	90	09-Jan-18 A	01-Sep-18	-160		
13434	ADB - External concrete pavement (EVA)	24	18-Jan-18 A	22-Sep-18	-60		
13436	ADB - External Fence Wal (include meta	al gate)	130	18-May-18 A	29-Sep-18	-11		
3254f	VO/209 - VO Works installation (Street fi EVA of ADB)	re hydrant and water connection at	30	19-Jul-18 A	15-Sep-18	-60		
Leve		ojour Badomino	-	ramme	e Upda	ate 54	(Asia) Limited (August 2018)Project ID: H2613-U054 Baseline: DWP4 Layout: Update Three Month Rollin U054 Page 16 of 27	g Date Revision Checked Approv 20-Jul-18 U053 AT CW 20-Aug-18 U054 AT CW

Data Date: 20-/	Aug-18	TASK		CWB(3: 3 Month							t HL.						
ctivity ID	Activity Name		Original Duration	Start	Finish	Total Float			•	•		2018	l				
3263b	VO/221 - Manholes by others to be modi	ified to match with the final road and		27-Jul-18A	22-Sep-18	-6			Aug		Sep			Oct	;	1	Nov
	paved levels		-10	27-00-107	22-06p-10	-0				 							
E&M Testir	ng &Commissioning / Statutory Insp	pection															
13446	MEP(ADB) - Statutory Inspection & Certi inspection) (Building)	ificates (include EMSD & FSD	7	12-Jun-18 A	21-Aug-18	-198											
13454a	MEP(ADB) - Use Permit - Lift (Non-FS)		0	16-Aug-18 A					•								
13458	MEP(ADB) - Submission of WWO46 (Pa	art IVA to WSD	0	20-Aug-18		-222											
				20 Aug 10													
KD03M7	MEP(ADB) - Milestone for KD06		0		25-Aug-18	22											
13460	MEP(ADB) - Submission of WWO46 (Pa	art V) to Client	0	10-Sep-18		-270					♦						
13446a	MEP(ADB) - Statutory Inspection & Certi EVA)	ficates (FSD inspection) (SFH &	2	24-Sep-18	26-Sep-18	-60						-					
Final Com	oletion Works																
13464	ADB - TCSS & other E&M systems Site A	Acceptance Test	18	02-May-18 A	29-Aug-18	-236											
13468	ADB - Tunnel FS operation test		30	20-Aug-18	18-Sep-18	-403						I					
KD05M8	TCSS SAT (ADB) - Milestone for KD05		0		29-Aug-18	18				 •							
13466	ADB - Completion of Section 1 (KD06)		0		18-Oct-18	-32		▲						•			
Landscapi	ng and Irrigation System																
13588	ADB - Final completion test for irrigation	systems in PortionXa and Xb	60	20-Aug-18	18-Oct-18	-433											
13590	ADB - Landscape Works in Portion Xa a	nd Xb	60	31-Oct-18	29-Dec-18	-469				 							
East Ventil	ation Shaft (EVS)																
ABWF Wo	ks																
3826	EVS - ABWF (Dry Trade)		60	20-Sep-17 A	25-Aug-18	18											
3830	EVS - Metal works / steel platform / Lado	lers / Handrails	48	19-Dec-17 A	01-Sep-18	12											
External Fa	acade																
19060	EVS -Cone louvre installation		60	07-Feb-17 A	30-Aug-18	-182		<u></u>	·	 •							
3832	EVS - Architectural Features of EVS		120	12-Jul-17 A	15-Sep-18	-178											
MEP Works	5																
		Т														1	
•		emaining Work oject Baseline	Leia	hton C	Contra	ctors	(As	ia) Li	mited	-	ect ID: H26			Date 20-Jul-18	Revisi U053	on Che AT	cked Approv CW
	velione Milestone	ojou Dadomio	-	ramme			•	-			line: DWP4	l Three Month	Rolling	20-Aug-18		AT	CW
	ual Work	╹			EE MO		-	-	-	U054			, coming				
Crit	cal Remaining Work			INK			nUL		2		17 of 27						

Data Date: 20-A	ug-18	TASK		CWB(ry, Not	HL.						
ctivity ID	Activity Name		Original Duration	Start	Finish	Total Float						2	2018					
3836	MEP(EVS) - E&M 1st Fix		12	05-Sep-17 A	23-Aug-18	-180	!		Aug	-		Sep			Oct			Nov
3838	MEP(EVS) - E&M 2nd Fix		12	20-Sep-17 A	28-Aug-18	-184												
19054	MEP(EVS) - Lightning protection system	installation and T&C	12	11-Oct-17A	30-Aug-18	-170												
3840	MEP(EVS) - E&M Final Fix		12	22-Aug-18	04-Sep-18	-184												
19056	MEP(EVS) - Features lighting installation	and T&C	24	31-Aug-18	28-Sep-18	-182				1								
3844	MEP(EVS) - E&M Individual System T&C		10	05-Sep-18	15-Sep-18	-184												
													_					
3846	MEP(EVS) - E&M Final Completion Wor	ks; Ready for Statutory Inspections	6	17-Sep-18	22-Sep-18	-184												
External W																		
3850	EVS - External concrete pavement		12	31-Aug-18	13-Sep-18	-170												
3854	EVS - Final completion works (include Co	CMS interface)	12	14-Sep-18	28-Sep-18	-182												
E&M Testin	g &Commissioning / Statutory Ins	pection																
3856	MEP(EVS) - E&M System Integrated Tes	sting and Commissioning	6	23-Sep-18	28-Sep-18	-230							_					
3858	MEP(EVS) - Ready for Statutory Inspect	ion (with EVB)	0	29-Sep-18		-229							•					
KD03M4	MEP(EVS) - Milestone for KD03		0		29-Sep-18	-12							٠					
Final Comp	Detion Works																	
3880	EVS - Completion of Section 1 (KD06)		0		29-Sep-18	-229							٠					
Satellite Co	ontrol Points 4 / 5																	
SCP4																		
3798	SCP4 - External Works		24	19-Mar-18 A	25-Jul-18 A													
10112	MEP(SCP4) - TCSS Enabling Works (Re	emaining TCSS installation)	18	04-Jul-18A	09-Aug-18 A													
3794	MEP(SCP4) - E&M Individual System T8	кС	12	25-Jul-18 A	14-Aug-18 A													
3796	MEP(SCP4) - E&M Final Completion W	orks; Ready for Statutory	12	07-Aug-18 A	17-Aug-18 A													
KD03M3	Inspections MEP(SCP4) - Milestone for KD06		0		17-Aug-18 A				•									
SCP5																		
Levi Levi Bas				ihton C ramme THRE		ate 54	1 (Au	igust	2018)	!	Baseli Layou U054	it ID: H2613- ne: DWP4 t: Update Th 18 of 27		Rolling	Date 20-Jul-18 20-Aug-1	_	sion Cheo AT AT	ked Approv CW CW

Data Date: 20-	Aug-18	TASK	filters	CWB(s: 3 Month							y, Not HL.					
ctivity ID	Activity Name		Original Duration	Start	Finish	Total Float				•	-	018				
3886	SCP5 - External Works		24	18-Jun-18 A	01-Sep-18	-211			Aug		Sep		Oct		No	v
			12													
10114	MEP(SCP5) - TCSS Enabling Works (Re			10-Jul-18A	08-Aug-18 A											
3882	MEP(SCP5) - E&M Individual System T8	C	12	20-Aug-18	01-Sep-18	-211										
3884	MEP(SCP5) - E&M Final Completion W Inspections	orks; Ready for Statutory	12	03-Sep-18	15-Sep-18	-211										
KD03M5	MEP(SCP5) - Milestone for KD06		0		15-Sep-18	0					•					
External W	orks															
Rumsey S	treet Flyover for Paymnet & Traff	ic Barrier														
5902b	RS - Modification of existing edge parape	et at Connaught Road	108	05-Feb-18 A	31-Jul-18 A											
5902d	RS - Removal of central divider and repla	ace with waterfilled barriers	120	10-Feb-18 A	31-Jul-18 A											
5902p	RS - Pavement tie-in works at CORC W	/B	30	14-Aug-18 A	15-Sep-18	-215										
5902g	RS - Install new directional sign		6	17-Sep-18	22-Sep-18	-215					_					
5902r	RS - Road pavement tie-in E/B and W/B	of CORC	6	24-Sep-18	02-Oct-18	-215										
5902q	RS - Road marking		6	24-Sep-18	02-Oct-18	-215										
5902m	RS - Demolish existing nosing and crush	aushion	48	15-Oct-18	10-Dec-18	-141										
						-225			1							
5904a	RS - Construct permanent parapet and r	losing	102	15-Oct-18	21-Feb-19											
5902n	RS - Paving works on Bridge B		12	30-Oct-18	12-Nov-18	-141										
Area A/B																
Area ATCS	S															
10288a3	Request for VO/instruction-TCSS equipr FVMS1 / ADS01) (Ref: H27613-LJV-ME		24	04-Oct-16A	25-Aug-18	-185										
Area B		,														
Area B TC	SS															
Approact	n Road / Landscape Deck / Noise Enc	losure (No TTA)														
10288b22	Area B TCSS cable termination (on IEC)	s Westbound) - DS06B	9	08-Jun-18 A	26-Jul-18 A											
10288b1	Area B TCSS equipment installation and Westbound) - GT3, GT2, Sm CCTV at 0	cable termination (on IEC's Grade	18	13-Jun-18A	15-Aug-18 A											
🔶 Cu	rrent Milestone	maining Work		hton C	ontra	otoro	(//	ia) I in	nitod		Project ID: H2613-I	U054	Date	Revision	_	d Approv
		ojour Badoomio	-				-	-			Baseline: DWP4			U053	AT	CW
	æline Milestone ual Work		rog	ramme	-		-	-	2018)		Layout: Update Thi	ree Month Rolling	20-Aug-18	0054	AT	CW
	ical Remaining Work			THRE	EE MO	NTH	ROL	LING			U054 Page 19 of 27					

Da	ta Date: 20-Ai	ug-18	TASK		CWB(3 Month									t HL.					
Activity	y ID	Activity Name		Original Duration	Start	Finish	Total Float				· 				2018		-		
	10288b2	Area B TCSS equipment installation and Eastbound) - CCTV & AID	cable termination (on IEC's	12	11-Jul-18A	07-Aug-18 A					Aug			Sep			Oct		Nov
	10288b36	Area B cabling along existing IECL sign g provision must be ready for cabling)	antries/bridge F3B (C19 civil	12	16-Jul-18 A	31-Jul-18 A			-										
	10288b38	Area B cabling along existing IECL sign g provision must be ready for cabling)	antries/bridge F2B (C19 civil	12	16-Jul-18 A	15-Aug-18 A					-								
	10288b4	Area B TCSS equipment Testing & Com	missioning	25	16-Aug-18 A	01-Sep-18	-203						-						
	NOC 163 -	Optical Fibre Damaged - Need to b	e Replaced (From Gantry ADS0	6 to ADB	Computer Roo	m)												 	
	10288b14	TCSS optic fibre order and delvery		48	25-Jun-18 A	24-Aug-18	-191												
	10288b14	Pull out damaged cable (Require TTA for	r 1 night shift)	2	25-Aug-18	27-Aug-18	-191					-							
	10288b14	Lay the new cable from gantry ADS06 to for 2 night shifts)	ADB Computer room (Require TTA	2	28-Aug-18	29-Aug-18	-191					•							
	10288b14	Cable termination at ADB Computer Roc	om (Require TTA for 2 night shifts)	2	30-Aug-18	31-Aug-18	-191												
	Noise Encl	osure (Live Traffic, TTA) - Night Shif	t																
	10288b6	Area B TCSS equipment installation and Westbound) - FADS06	cable termination (on IEC's	10	18-Jun-18 A	15-Aug-18 A													
	10288b8	Area B TCSS equipment Testing & Comr	missioning	20	11-Jul-18A	30-Aug-18	-201												
	10288b10	Area B TCSS equipment installation and Eastbound) - FADS08A (Works deleted)	cable termination (on IEC's	6	31-Jul-18 A	31-Jul-18 A			•										
	Existing IE	C (Live Traffic, TTA) - Night Shift																	
	10288b26	Area B TCSS equipment Testing & Comr	nissioning	12	31-Aug-18	13-Sep-18	-201												
	Area B Tunn																		
		Deck (Bay C1 to C5)																	
	Landscap	e Deck (Bay C1 & C2A-2 Remaining	Bay (W/B))																
		Cable laying / DALI wiring and cable term	nination	40	18-Jun-18 A	21-Jul-18A		-										 	
		Handover to C19 for Asphalt pavement		6	23-Jul-18 A	29-Jul-18 A													
		T&C and energisation		6	20-Aug-18	25-Aug-18	-203	_	-			_							
		LUX measurement		18	27-Aug-18	15-Sep-18	-203			—		_							
		e Deck (Bay C1 & C2A-2 Remaining																	
	10288c40	Cable laying / DALI wiring and cable tern	nination	40	12-Jun-18A	04-Aug-18 A													
	Leve			-	hton C ramme THRE		te 54	Ì (Aı	ugus	st 20			Base Layo U054	•		Rolling	Date 20-Jul-18 20-Aug-1	on Che AT AT	cked Approv CW CW

Dat	a Date: 20-A	ug-18	TASK					missioning Contract Original Sections, No Summary, Not HL.	
ctivity	ID	Activity Name		Original Duration	Start	Finish	Total Float		
	10288c44	Handover to C19 for Asphalt pavement		6	23-Jul-18 A	29-Jul-18 A		Aug Sep Oct Nov	
	10288042	T&C and energisation		3	16-Aug-18 A	25-Aug-18	-203		
	10288c46	LUX measurement		18	27-Aug-18	15-Sep-18	-203		
	Landscap	e Deck (Bay C2A-1 to B1 & C3 Bay (W/B))						
	10288c54	T&C and energisation		6	20-Aug-18	25-Aug-18	-209		
	10288c56	Handover to C19 for Asphalt pavement		6	27-Aug-18	01-Sep-18	-209		
	10288c58	LUX measurement		18	03-Sep-18	22-Sep-18	-209		
	Landscap	e Deck (Bay C2A-1 to B1 & C3 Bay (E/B))						
	10288c68	T&C and energisation		6	20-Aug-18	25-Aug-18	-209		
	10288c70	Handover to C19 for Asphalt pavement		6	27-Aug-18	01-Sep-18	-209		
	10288c72	LUX measurement		18	03-Sep-18	22-Sep-18	-209		
	Landscap	e Deck (Bay C4 - E/B Slow Lane)							
	10288c80	Cable laying / DALI wiring and cable term	nination	24	11-Jul-18 A	21-Aug-18	-211		
	10288c82	T&C and energisation		6	22-Aug-18	28-Aug-18	-211		
	10288c90	Handover to C19 for ADS08A sign face in	nstallation / Asphalt pavement	18	29-Aug-18	18-Sep-18	-211		
	10288c86	LUX measurement		6	19-Sep-18	26-Sep-18	-211		
	Landscap	e Deck (Bay C4 - E/B Fast Lane)							
	10288c96	Cable laying / DALI wiring and cable term	nination	30	13-Jul-18 A	18-Aug-18 A			
	10288c104	Lighting / Conduit installation (continue)		6	24-Jul-18 A	30-Jul-18 A			
	10288c98	T&C and energisation		6	19-Aug-18 A	25-Aug-18	-203		
	10288c100	LUX measurement		18	27-Aug-18	15-Sep-18	-203		
	Landscap	e Deck (Bay C4 - W/B)							
	10288c110	Cable laying / DALI wiring and cable term	nination	36	17-Jul-18 A	25-Aug-18	-209		
	10288c156	C19 - Remaining works / Asphlt Paving a	nd Road Marking	24	20-Aug-18	15-Sep-18	-215		
A	Leve			-	ramme	e Upda	ate 54	s (Asia) Limited 4 (August 2018) ROLLING	»V

Duto.	20-Aug-18	TACI	(filton	CWB(s: 3 Montl																		
	Activity Name	TASI		S: 3 MONTI	IS_4, 3IVIF	Total Float	Jrigin	nal Se	ection	IS, NO	Sumn	nary, N	IOT HL	•								
)	Activity Name		Original Duration		FILIST	Iotal Float				Aug				20 Sep	18	1	Oct				Nov	
102	88c78c C19 - demolition of concrete structur	e (dolphin) - need further 1 week	6	27-Aug-18	01-Sep-18	-209	1			, lug	•											
102	88c112 T&C and energisation		6	10-Sep-18	15-Sep-18	-215								•								
102	88c114 LUX measurement		18	10-Sep-18	02-Oct-18	-215							_									
Land	iscape Deck (Bay C5 - E/B Slow Lane)																				
102	88c78; Handover to C19 for remaining work	s at Bay C5 - E/B Slow Lane	34	01-Jun-18A	23-Jul-18 A		<u> </u>															
	88c124 Cable laying / DALI wiring and cable		24			-200																
				12-Jul-18 A	22-Aug-18										ļ							
102	88c12€ T&C and energisation		6	23-Aug-18	29-Aug-18	-200			-													
102	88c128 LUX measurement		18	23-Aug-18	12-Sep-18	-200			-			-										
Land	iscape Deck (Bay C5 - E/B Fast Lane)																					
102	88c78a Handover to C19 for remaining work	s at Bay C5 - E/B Fast Lane	34	01-Jun-18A	23-Jul-18 A		-															
102	88c124 Cable laying / DALI wiring and cable	termination (continue)	24	24-Jul-18 A	27-Aug-18	-204																
102	88c13£ T&C and energisation		6	28-Aug-18	03-Sep-18	-204						 										
102	88c14(LUX measurement		18	28-Aug-18	17-Sep-18	-204			_				_	-								
Land	iscape Deck (Bay C5 - W/B)																					
102	88c78 Handover to C19 for remaining work	s at Bay C5 - W/B	34	25-May-18 A	24-Jul-18 A		÷															
102	88c124 Conduit installation (continue)		6	25-Jul-18 A	31-Jul-18 A																	
	88c14{ Cable laying / DALI wiring and cable	termination	30	08-Aug-18 A	01-Sep-18	-209									+							
	88c15(T&C and energisation		6	03-Sep-18	08-Sep-18	-209			-													
102	88c152 LUX measurement		18	03-Sep-18	22-Sep-18	-209			-			- -										
	aining Area (TTA Required) - Night Sh																					
Wes	tBound																					
1902	22 Area B (Remaining need TTA) - Ligh	ting power cable laying (High Level)	12	20-Jul-18 A	30-Jul-18 A			-														
1902	24 Area B (Remaining need TTA) - Cat	le termination (High Level)	8	31-Jul-18 A	04-Aug-18 A																	
1902	26 Area B (Remaining need TTA) - Test	ing & Energization	6	05-Aug-18 A	11-Aug-18 A																	
•																	Dat	te T	Revisi	ion ICh	ecked	Ann
	Current Milestone Level of Effort	Remaining Work Project Baseline		ghton (oject ID: l aseline: D		054		20-Jul		U053	AT		CW
				jrammo									asenne. D ayout: Upo		a Month	Rolling	20-Au			AT		CW
	Actual Work									J.J))54			litoling		J . V				12.1
	Critical Remaining Work			IHK	EE MO	IN I H	кU	LLIP	NG				age 22 of	07								

Data Date: 20-A	.ug-18	TASK						oning Cont		Not HL									
Activity ID	Activity Name	I	Original Duration	Start	Finish	Total Float					20	18	I						
	l load Widening (Bridge A / Mar		Balation				: :	Aug	; ;	;	Sep		; ;	(Oct		÷	Nov	
		TFO Sueety																	
Approval / A	Access																		
RW0002	XP application		35	04-Jun-18 A	27-Jul-18 A														
RW0008	MTR consent for apply additional loading	(RSS to assist)	48	11-Jun-18 A	15-Aug-18 A														
RW0012	TMLG approval for works at Man Po Str	eet	48	28-Jun-18 A	27-Jul-18 A														
RW0010	TMLG approval for works at Man Kwong	g Street	18	09-Jul-18 A	25-Jul-18 A														
RW0014	Gantry shop drawings preparation		48	20-Aug-18	16-Oct-18	-78		-				:			•				
Procuremer	nt / Manufacturing / Deliveries																		
RW0018	Works sublet (include all trades)		48	04-Jun-18A	01-Sep-18	-84													
RW0022	Re-order of TCSS cables and sign faces	etc.	50	20-Aug-18	19-Oct-18	-98		-							-				
RW0020	Gantry fabrication & delivery		54	18-Oct-18	19-Dec-18	-78									_	_			
Construction	n / Installation Works																		
RW0024	Surverys		24	27-Jul-18 A	04-Aug-18 A		-												
RW0026	UU diversion		114	06-Aug-18 A	05-Dec-18	-126										_			_
RW0028	RC demolition (assume all demolition in o	daytime)	72	20-Aug-18	14-Nov-18	-96		-											
RW0030	RC construction		96	17-Sep-18	12-Jan-19	-96					_					_			
RW0032	Gantry removal (flyover full closure once	per week)	18	18-Oct-18	07-Nov-18	-42									_				
NOC 159 - N	Modification Works for Niche	A2 (FSD Requirements) - R	FV/483																
192008	Install MCB boards and cabling works		27	16-Jul-18 A	14-Sep-18	-219					•								
192012	Manufacture new access doors / frames		40	16-Jul-18 A	02-Oct-18	-68													
192022	Remove existing VE panels		12	16-Jul-18A	28-Aug-18	-214													
192010	Fire rated protection works		24	25-Aug-18	21-Sep-18	-219						I							
192014	Install new access doors / frames		12	03-Oct-18	16-Oct-18	-68									•				
192016	Measure infill panels and manufacture pa	ermanent infill panels	32	18-Oct-18	23-Nov-18	-68									_				-
Curra	ent Milestone	emaining Work			_	_				Droject ID:		1054	;!		Date	Revi	sion Che	cked Appro)V
-		oject Baseline	Leig	nton C	contra	ctors	(Asia	a) Limited		Project ID: Baseline: [1004			20-Jul-18	U053	AT	CW	
▲ ▲ Base	eline Milestone	P	roa	ramme	e Upda	ite 54	l (Aud	gust 2018)		Layout: Up		ee Month	n Rollina	-	20-Aug-18		AT	CW	
	ial Work al Remaining Work		9		EE MO					U054 Page 23 of				-			I	I	

Data Date: 20-A	ug-18	TASK					nissioning Conti Original Sections, No S		t HL.				
ctivity ID	Activity Name		Original Duration	Start	Finish	Total Float			2018	1			
	ions affect TCSS Works at Exter						Aug		Sep	Oc	t		Nov
		nu Alcus											
Sheung wa	In to Western Portal												
191593	Install 2xVMS 6 and 2xTSG near FADS01 a	and SCT	24	17-Jul-18 A	13-Aug-18 A								
Wan ChaiA	Area												
191597	Install TCSS cabinet and CCTV and SCT		24	15-Jul-18 A	25-Aug-18	-256							
Tin Hau Are	a												
191601	Install TCSS fiend equipment / cable termin	ation and SCT	24	15-Jul-18 A	25-Aug-18	-256							
					20 / kig 10	200							
North Point	Area												
191605	Install 2x VSLS at the Eastern Portal and Se	СТ	24	15-Jul-18 A	18-Aug-18 A								
191609	Install VMS4 and TSG at C19 area and SC	Т	24	15-Jul-18 A	25-Aug-18	-256							
TCSS Syste	m Installation and Connection	Works for HyD, TD and H	KPF										
12798	TCSS system installation and connection we	orks for Sub ETCC at Mong Kok	7	08-Aug-18 A	22-Aug-18	-229							
12800	Reginal Offices, TD TCSS system installation and connection we	orks for Emergency Coordination	7	08-Aug-18 A	22-Aug-18	-229							
	Centre at North Point HyD												
12802	TCSS system installation and connection we	orks for Hong Kong Police Force	7	10-Aug-18 A	22-Aug-18	-229							
12804	TCSS system installation and connection we Control Centre in Hong Kong Island	orks for Regional Command and	7	13-Aug-18 A	22-Aug-18	-229							
12806	TCSS system installation and connection we Regional Higher Command	orks for Hong Kong Island	7	14-Aug-18 A	22-Aug-18	-229							
12796	TCSS system installation and connection we	orks for Main ETCC at Wan Chai	7	16-Aug-18 A	22-Aug-18	-229							
Commissio													
For Tunnel	Opening												
9900d			69	00 May 10 A	00 Con 10	000							
	Route-wide TCSS Overall System SAT (OC		68	03-May-18 A	28-Sep-18	-266							
10016c1	FSD inspection (Tunnel Stage 1)		14	31-May-18 A	21-Aug-18	-181							
9900	Integrated System Test		42	23-Jul-18 A	06-Sep-18	-267							
9900d1	Emergency phone system / Radio system S	AT	24	20-Aug-18	12-Sep-18	-59	-						
10016c2	FSD inspection (Tunnel Stage 2)		12	03-Sep-18	15-Sep-18	-214							
											<u> </u>		
-		aining Work	Leia	hton C	ontra	ctors	(Asia) Limited		ect ID: H2613-U054		Date Rev		ked Approv
			-				(August 2018)		eline: DWP4		-Jul-18 U053	AT	CW
	eline Milestone al Work	F	nug		-				out: Update Three Month	Rolling 20	-Aug-18 U054	AT	CW
	al Remaining Work			THRE	E MO	NTH	ROLLING	U054 Page	4 e 24 of 27				
									-				

Data Date: 20-A	ug-18	TASK					nissioning Contract Driginal Sections, No Summa	ry, Not HL.					
ctivity ID	Activity Name		Original Duration	Start	Finish	Total Float		2018					
10016c3	FSD inspection (Tunnel Stage 3)		12	03-Sep-18	15-Sep-18	-220	Aug	Sep	Oct Nov				
10288b34	Area B TCSS Pre-test (Individual gantrie	s at existing IEC)	2	12-Sep-18	13-Sep-18	-251							
10016a	Remaining FSI and TSES inspection / De	efects re-inspection / LHDS / MFCP /	12	17-Sep-18	02-Oct-18	-220							
10016d	Niche A2 DCP FSD inspection for SCB and SCPs		1	17-Sep-18	17-Sep-18	-211							
	•												
12826a	Routewide FSD Inspection - Tunnel FS c		12	21-Sep-18	02-Oct-18	-77							
10016c4	Tunnel - Hot smoke test (1 test location of	nly)	2	24-Sep-18	26-Sep-18	-220							
10016c5	Tunnel - For mal Hot smoke test with FSL	Owtness	2	27-Sep-18	28-Sep-18	-220							
10016e	Issue of the FS Certificate from the FSD		0		08-Oct-18	-276		•					
KD05M1	Milestone for KD05		0		13-Oct-18	-27							
10016b	Ready for Tunnel opening		0		13-Oct-18	-281							
10016b2	Anticipated tunnel opening		0		13-Oct-18	-281							
APS Efficier	ncy Test / TCSS Operability Test	/ Establishment											
10194	Operability Test Plan submission		24	14-Sep-18	13-Oct-18	-101							
9910a	Arrangement of the Efficiency Test with T	D and the tunnel operator	30	14-Oct-18	12-Nov-18	-88							
10194a	Operability Test Plan Approval		24	15-Oct-18	12-Nov-18	-101	=						
9920	Operability Tests for TCSS		61	13-Nov-18	12-Jan-19	-118							
9910b	Record the APS efficiency		10	13-Nov-18	22-Nov-18	-88							
Training / P	lan / Manual for Project Comp	letion											
10128	Operation Training		100	01-Nov-18	07-Mar-19	-136							
Operation N	Ianual for CWB Opening												
10198a	Operation Manual for CWB opening - Dr	aft submission (Cost Centre 9C.	24	27-Dec-17 A	01-Sep-18	-36							
10198	9D) Operation Manual for CWB opening - Dr	aft submission (Cost Centre 9A. 9B)	12	20-Aug-18	01-Sep-18	-100							
10198b	Operation Manual for CWB opening - Dr	aft submission (Cost Centre 9E. 9F)	12	03-Sep-18	15-Sep-18	-36							
10198c	Operation Manual for CWB opening - Dr	aft submission (Cost Centre 9G)	12	03-Sep-18	15-Sep-18	-36							
Curre	ent Milestone	maining Work	مام	hton (ontro	otoro	(Asia) Limitad	Project ID: H2613-U054	Date Revision Checked Approv				
			-				(Asia) Limited	Baseline: DWP4	20-Jul-18 U053 AT CW				
	line Milestone al Work	F	rug		-		(August 2018)	Layout: Update Three Month Rolling U054	20-Aug-18 U054 AT CW				
	al Remaining Work			IHKE		NIH	ROLLING	Page 25 of 27					

Data Date: 20-A	ug-18	TASK						Dining Cont		y, Not HL.					
Activity ID	Activity Name		Original Duration	Start	Finish	Total Float			-		2018				
								Aug		Sep	2010		Oct		Nov
10198d	Operation Manual for CWB opening - Dr	aft submission (Cost Centre 9H, 9I)	12	03-Sep-18	15-Sep-18	-36									
191281	Operation Manual for CWB opening - Dr	aft (Cost Centre 9A. 9B) Approval	12	03-Sep-18	15-Sep-18	-100									
19128a1	Operation Manual for CWB opening - Dr	aft (Cost Centre 9C. 9D) Approval	12	03-Sep-18	15-Sep-18	-24									
10196a	Operation Manual for CWB opening - Fin	nal submission (Cost Centre 9C, 9D)	12	17-Sep-18	02-Oct-18	-24		+				•			
19128b1	Operation Manual for CWB opening - Dr	aft (Cost Centre 9E. 9F) Approval	12	17-Sep-18	02-Oct-18	-36		÷		-					
19128c1	Operation Manual for CWB opening - Dr	aft (Cost Centre 9G) Approval	12	17-Sep-18	02-Oct-18	-36									
19128d1	Operation Manual for CWB opening - Dr	aft (Cost Centre 9H, 9I) Approval	12	17-Sep-18	02-Oct-18	-36			-			•			
10196	Operation Manual for CWB opening - Fin	nal submission (Cost Centre 9A, 9B)	12	03-Oct-18	16-Oct-18	-60	-		•				-		
10196b	Operation Manual for CWB opening - Fin	nal submission (Cost Centre 9E, 9F)	12	03-Oct-18	16-Oct-18	-36							-		
10196d	Operation Manual for CWB opening - Fin	nal submission (Cost Centre 9H, 9I)	12	03-Oct-18	16-Oct-18	-36					4				
19196a1	Operation Manual for CWB opening - Fin	nal (Cost Centre 9C, 9D) Approval	12	03-Oct-18	16-Oct-18	-24							-		
101961	Operation Manual for CWB opening - Fin	nal (Cost Centre 9A, 9B) Approval	12	18-Oct-18	31-Oct-18	-60			_						
19196b1	Operation Manual for CWB opening - Fin	nal (Cost Centre 9E, 9F) Approval	12	18-Oct-18	31-Oct-18	-36			_						
19196d1	Operation Manual for CWB opening - Fin	nal (Cost Centre 9H, 9I) Approval	12	18-Oct-18	31-Oct-18	-36									
10196c	Operation Manual for CWB opening - Fin	nal submission (Cost Centre 9G)	12	01-Nov-18	14-Nov-18	-60									
19196c1	Operation Manual for CWB opening - Fin	nal (Cost Centre 9G) Approval	12	15-Nov-18	28-Nov-18	-60									
Training Pla	n for CWB Opening														
10206	Training Plan for CWB opening - Draft su	ıbmission	18	12-Sep-17 A	25-Aug-18	-144									
10206a	Training Plan for CWB opening - Draft a	oproval	18	27-Aug-18	15-Sep-18	-136									
10208	Training Plan for CWB opening - Final su	lomission	18	17-Sep-18	09-Oct-18	-136				-					
10208a	Training Plan for CWB opening - Final ap	pproval	18	10-Oct-18	31-Oct-18	-136		₽							
Training Ma	terial for CWBOpening														
10210	Training Material for CWB opening - Dra	ft submission	18	15-Nov-17 A	25-Aug-18	-144									
10210a	Training Material for CWB opening - Dra	ft approval	18	27-Aug-18	15-Sep-18	-144									
Leve		Jour Badonino	-	ramme		ate 54	l (Auç	a) Limited gust 2018) _ING		Project ID: H261: Baseline: DWP4 Layout: Update T U054 Page 26 of 27			Date Rev 20-Jul-18 U053 20-Aug-18 U054	AT	CW CW

Data Date: 20	-Aug-18		Data Date: 20-Aug-18 CWB(CC) - Commissioning Contract TASK filters: 3 Months_4, 3MRP, No Original Sections, No Summary, Not HL.																
Activity ID	ID Activity Name Original Start Finish Total Float														Oct	N	Nov		
10212	Training Material for CWB opening - Final sul	omission 18	17-Sep-18	09-Oct-18	-144			Aug			Gep								
10212a	Training Material for CWB opening - Final ap	proval 18	10-Oct-18	31-Oct-18	-136		7												
Maintena	nce Manual / Plan																		
10200	Maintenance Plan	18	10-Oct-18	31-Oct-18	-144		-							-					
10220	Maintenance Manual / logbook - Draft submis	sion 18	01-Nov-18	21-Nov-18	-144														

Current Milestone	Remaining Work	Laighton Contractors (Asis) Limited	Project ID: H2613-U054	Date	Revision	Checked	Approv
Level of Effort	Project Baseline	Leighton Contractors (Asia) Limited	Baseline: DWP4	20-Jul-18	U053	AT	CW
▲ ▲ Baseline Milestone		Programme Update 54 (August 2018)	Layout: Update Three Month Rolling	20-Aug-18	U054	AT	CW
Actual Work		THREE MONTH ROLLING	U054				
Critical Remaining Work			Page 27 of 27				
