## KINGSFORD ENVIRONMENTAL (H.K.) LTD.

Consultancy Engineering & Contracting



#### CONTRACT NO. DE/2005/03

SUPPLY AND INSTALLATION OF ELECTRICAL AND MECHANICAL EQUIPMENT FOR EXPANSION OF SHEK WU HUI SEWAGE TREATMENT WORKS

#### ENVIRONMENTAL MONITORING AND AUDIT

## MONTHLY EM&A REPORT NO. 37

**JUNE 2009** 

for

**Biwater Man Lee Limited** 

Submitted by

Kingsford Environmental (H.K.) Ltd.

CONTROLLED DOCUMENT

Revision: A

Revision Date: 3/7/09

Approved by: SL

Distribution Date: 3/7/09

CUSTC	MER:	Biwater Man Le	ee Limited		
PROJE	CT <b>NAME</b> :	# # V		al and Mechanical l e Treatment Works	
PROJE	CT NO.:	81869			
Author:		T. Y. Yearno (Signature)  Date: 3/7/2009		Mr. Tony Yeung (Name)	5
Review	and Approved by	: (Signature) - Date: 3/7/2009	<u></u>	Mr. Stanley Lau (Name)	
CONTE	ROLLED DOCUI	MENT DISTRIBU	TION		
Documen	nt Title : 1	Monthly EM&A Rep	ort No. 37	Controlled Copy N	lo.:
Docume	nt No. : 1	RPT:MRPTNo.37Re	vA/81869		
Distribut	ed to : 1	Biwater Man Lee Lin	nited	Date	: 3/7/2009
		RI	EVISION RECORD		
Rev. No.	Revision 1	Notification	Date	Approved By	Signature

REVISION RECORD					
Rev. No.	Revision Notification	Date	Approved By	Signature	
A	Report issued to Client	3/7/2009	Stanley Lau	1///2	
				/	
				1	

#### TABLE OF CONTENTS

## Approval & Distribution Sheet Executive Summary

- Work Activities during the Month
- 3 Status of Environmental Protection
- 4 Site Inspections
- 5 Summary of Deficiencies and Remedial Actions
- 6 Summary of Complaints and Remedial Actions
- 7 Summary of Summons and Prosecutions
- 8 Monthly Environmental Auditing for the Coming Months
- 9 Conclusions and Comments

#### Tables:

- Table 1 Work Activities for June 2009
- Table 2 Status of Permits and Licenses
- Table 3 Type and Quantity of Waste Disposed of in June 2009

#### Appendices:

- 1 Contact Information of Key Environmental Personnel
- 2 Sensitive Receivers, Locations of Monitoring and Control Stations, Action and Limited Levels and Event/Action Plan
- 3 Construction Programme
- 4 Environmental Requirements and Implementation Status
- 5 Site layout plan and Site Inspection Checklists
- 6 Deficiency Investigation Reports
- 7 Complaint Reports
- 8 Summons and Prosecutions Records
- 9 Permits

Doc. No.: RPT:MRPTNo.37/RevA/81869

#### APPROVAL & DISTRIBUTION SHEET

DOCUMENT DATE: 3 July 2009

APPROVAL

Certified by: ET Leader

Signature:

Mr. Stapley Lau

Date: 3/7/09

#### DISTRIBUTION LIST

Title	Name	No. of Copies
Engineer's Representative (Drainage Services Department)	Mr. K.K. Cheung	8
E&M Contractor (Biwater Man Lee Limited)	Mr. Frankie Chan	1
Independent Environmental Checker (CH2M HILL Hong Kong Limited)	Mr. Y. T. Tang	1

#### **EXECUTIVE SUMMARY**

This is the thirty-seventh monthly Environmental Monitoring and Audit (EM&A) Report for the Drainage Services Department Contract No. DE/2005/03 entitled "Supply and Installation of Electrical and Mechanical Equipment for Expansion of Shek Wu Hui Sewage Treatment Works". This report contains the results of the environmental monitoring for verification of mitigation implementation conducted by the Environmental Team (ET) of the E&M Contractor as required in the contract.

For the environmental monitoring activities, Action and Limit (A/L) Levels are defined levels of impact recorded which represent levels at which a prescribed response is required. Action Limit is an indication of a deteriorating ambient environment for which appropriate remedial actions are likely to be necessary to prevent environmental quality from falling outside the Limit Levels. If these are exceeded, construction works should not be preceded without appropriate remedial action, including critical review of the methods. Baseline monitoring was conducted by the Civil Contractor in December 2005 (Report No. 01284R0012).

The activities in this month consisted of E&M installation and testing of Filter Press & associated system at Filter Press House Extension (Section 9). Cabling work for Waste Gas Burner is commenced (Section 10). The defects rectification of SAS thickening system in SAS Consolidation House (Section 5) and BR5 unit & associated equipment (Section 6, 7 & 8) was in progress.

Site inspections by an Environmental Team were carried out on 4, 8, 16, 24 and 30 of June 2009 with the representatives of the Engineer. Joint site audit was conducted on 10 June 2009 with the representatives of Engineer, IEC, E&M Contractor and ET.

No deficiency was found during the site inspections in June 2009. Work activities and mitigation measures were in compliance with the environmental protection regulations, contract requirement and environmental permit.

The monthly EM&A meeting was held on 10 June 2009 with all of the parties (DSD, E&M contractors, ETs, and the IEC) involved.

There was no EPD visit during June 2009 and no abatement notice or prosecution was raised by EPD.

There was no complaint received or notification of summons or successful prosecution in June 2009.

There was no reporting change during the reporting month.

The planned activities for July 2009 - September 2009 as regards E&M equipment are mainly the Installation and Testing & Commissioning (if required) for i) Filter Press at New Press House Extension, ii) Sludge Conditioning Tank Nos.3 & 4, iii) Ferric Chloride Storage Tank at Bunded Area, iv) Deodourizers at Inlet Work & Sludge Holding Tanks, v) Waste Gas Burner; Defects for SAS Thickening System in SAS Consolidation House (Section 5) and BR5 unit & associated equipment (Section 6, 7 & 8) are scheduled to rectify.

CONTROLLED DOCUMENT

Doc. No.: RPT:MRPTNo.37/RevA/81869

#### 1 Introduction

This is the thirty-seventh monthly Environmental Monitoring and Audit (EM&A) Report for the Drainage Services Department Contract No. DE/2005/03 entitled "Supply and Installation of Electrical and Mechanical Equipment for Expansion of Shek Wu Hui Sewage Treatment Works". The report was prepared by the Environmental Team, Kingsford Environmental (H.K.) Ltd., of the E&M Contractor, Biwater Man Lee Limited. This report is submitted to the Client, the Drainage Services Department, and the Independent Environmental Checker, CH2M HILL Hong Kong Limited, for the project. In addition, this report will be submitted to EPD in accordance with the requirement of the environmental permit (EP218-2005) and EM&A manual of the project.

This report only presents the results of the environmental auditing of the project activities regarding the E&M equipment installation conducted in the month of June 2009. The auditing works include regular site inspections for verification of the mitigation measures implementation as recommended in the EM&A Manual and as detailed in the Project Profile for the project.

The contact information for the key personnel is shown in Appendix 1.

The job nature of the E&M contractor is mainly for installation of E&M equipment, all hand-held's breakers, bulldozer, concrete lorry mixer, dump truck and hand-held's poker, vibratory would not be frequently used so that the impact from noise and dust would be low. Also, the distance to the nearest sensitive receivers is long. Therefore, the potential environmental impact imposed to the sensitive receivers would be low. Routine environmental monitoring would be considered when deficiency is found or complaint is received.

The sensitive receivers, locations of monitoring and control stations, action and limited levels and event/action plan are shown in Appendix 2.

#### 2 Work Activities during the Month

The activities in this month consisted of E&M installation and testing of Filter Press & associated system at Filter Press House Extension (Section 9). Cabling work for Waste Gas Burner is commenced (Section 10). The defects rectification of SAS thickening system in SAS Consolidation House (Section 5) and BR5 unit & associated equipment (Section 6, 7 & 8) was in progress.

The activities and dates of occurrence of each activity are summarized below in Table 1. The Construction Program is shown in Appendix 3.

Table 1: Work Activities for June 2009

SAS Consolidation House					
Defects rectification of SAS thickening system	7 May 08 – 6 May 09*				
Air Blower House No.2					
Installation of E&M equipment	1 Apr 08 – 3 Nov 08*				
Testing and commissioning of Air Blowers	4 Nov 08 – 28 Nov 08*				
Defects rectification of Air Blowers	29 Nov 08 – 29 Nov 09*				
Bioreactor No.5					
Installation of E&M equipment	18 Mar 08 – 30 Oct 08*				
Testing and commissioning	1 Nov 08 – 23 Feb 09*				
Defects rectification of Bioreactor No.5	24 Feb 09 – 23 Feb 10*				
Flow Division Pump Pit No.1 (FD1)					
Installation of E&M equipment	18 Mar 08 – 30 Oct 08*				
Testing and commissioning	1 Nov 08 – 23 Feb 09*				
Defects rectification of FD1	24 Feb 09 – 23 Feb 10*				
Flow Division Pump Pit No.2 (FD2)	Flow Division Pump Pit No.2 (FD2)				
Installation of E&M equipment	8 Sept 08 – 15 Nov 08*				
Testing and commissioning	16 Nov 08 –23 Feb 09*				
Defects rectification of FD2 24 Feb 09 – 23 Feb 10*					
Switch Room for RAS/SAS Pumping Station No. 2					

CONTROLLED DOCUMENT

Doc. No.: RPT:MRPTNo.37/RevA/81869

11 Apr 08 – 15 Nov 08*				
8 Nov 08 – 23 Feb 09*				
24 Feb 09 – 23 Feb 10*				
28 Apr 08 – 15 Nov 08*				
16 Nov 08 – 23 Feb 09*				
24 Feb 09 – 23 Feb 10*				
Final Sedimentation Tank (FST) Nos. 9 & 10				
11 Apr 08 – 14 Dec 08*				
15 Dec 08 – 23 Feb 09*				
24 Feb 09 – 23 Feb 10*				
Sludge Press House Extension				
18 July 08 – 17 May 09*				
18 May 09 – 10 July 09*				
Deodourizers & Waste Gas Burner				
18 July 08 – 17 July 09*				

<sup>\*</sup> Scheduled dates only for completion of the activities

#### 3 Status of Environmental Protection

#### Air Quality

Appropriate mitigation measures for the activities are in place. Plastic covers with stakes/weights are readily available and used for covering of exposed material for control of dust. Water spray is available for dust suppression, if necessary.

# tallation of Electrical and Mechanical Equipment for Revision: A hek Wu Hui Sewage Treatment Works Rev. Date: 3/7/09

Contract No. DE/2005/03

#### Water Quality

The plastic covers for exposed soil, etc. are available for minimization of silt in the run-off water during rainstorms, if necessary. Sandbags will be provided for preventing surface run-off discharging directly into public drain area. Note that wastewater generated from the off-site project office was collected in a storage tank and tanker-away regularly by a licensed collector.

Anti-mosquito preventive measures, e.g. regular removal of stagnant water (if possible) and/or spraying larvicide (if necessary) at any site area, are taken for mosquito control and prevention, particularly for control of Dengue Fever and Japanese Encephalitis diseases.

#### Noise

Plants with low noise emittance are preferred and are operated / maintained to reduce noise. In this reporting month, work was carried out during normal working hours (7am – 7pm Monday to Saturday) or otherwise specified in the contract. In the event of a schedule change such that construction work would be performed during the restricted hours (11pm – 7am and during general public holidays including Sundays), a Construction Noise Permit would be required.

#### Waste / Chemical Management

The construction waste materials are preferred to be removed promptly from the site. Recyclable hard inert C&D materials should be taken to a public filling area (Tuen Mun Area 38) whereas the non-inert C&D waste should be disposed of to WENT landfill at Nim Wan or other disposal site approved by the control authority. Note that the inert C&D materials should be reduced, reused and recycled if possible, before disposal. Any substance identified as chemical waste would be disposed of properly by a licensed collector. A trip ticket system for the disposal of C&D waste should be conducted as required by the Waste Management Plan. Rubbish bins are provided on-site for collecting general refuses as necessary. The general refuse would be removed regularly and disposed to landfills by a licensed collector. A proper record of each waste disposal, including the new bar-coded disposal delivery form, would be kept to verify proper handling and disposal.

The status of permits and licenses is summarized in Table 2 and shown in Appendix 9.

Table 2: Status of Permits and Licenses

Description	Permit No.	Valid Period		Ref.	Status	
		From	To			
Environmental Permit	EP-218/2005	16/06/05	End of Project	PS1.39*	Granted	
Register as Chemical Waste Producer	WPN 5517-624-B1 039-02	14/06/07	End of Project	Waste Disposal (Chemical Waste) (General) Regulation (Cap. 354)	Granted	

<sup>\*</sup> Particular Specification of Contract No. DE/2005/03

The implementation status of mitigation measures from EM&A Manual is attached in Appendix 4.

#### 4 Site Inspections

Site inspections by an Environmental Team were carried out on 4, 8, 16, 24 and 30 of June 2009 with the representatives of the Engineer. Joint site audit was conducted on 10 June 2009 with the representatives of Engineer, IEC, E&M Contractor and ET.

The inspected site locations were marked on a site layout plan and the location code was recorded on the checklist. The site layout plan is shown in Appendix 5.

The activities in this month consisted of E&M installation and testing of Filter Press & associated system at Filter Press House Extension (Section 9). Cabling work for Waste Gas Burner is commenced (Section 10). The defects rectification of SAS thickening system in SAS Consolidation House (Section 5) and BR5 unit & associated equipment (Section 6, 7 & 8) was in progress.

No deficiency was found during this month. Inspection checklists are annexed in Appendix 5. Whereas all of the environmental aspects were inspected in the work areas, the most applicable descriptions are addressed below.

#### Air Quality

No dusty material was found from the site areas or activities this month.

#### Water Quality

No surface run-off was observed during the site inspections this month. Note that the regular inspections and preventive measures for the mosquitoes are being conducted and recorded at least weekly by the Contractor.

#### Noise

During this month, the work activities and equipment used did not generate significant noise. In this reporting month, no work was carried out during general public holidays including Sundays.

#### Waste / Chemical Management

Refuse bins and waste storage/sorting area were provided for the collection of general refuse and sorting the C&D materials.

Construction waste was disposed to the WENT landfill by the licensed waste collector on 8 June 2009.

The type and quantity of waste for final disposal during June 2009 is shown in Table 3. Note that a record of each disposal is being kept.

Table 3: Type and Quantity of Waste Disposed of in June 2009

Types of Waste	Quantity
Inert C&D Material	Nil
Non-inert C&D Waste	1.43 tons
Chemical Waste	Nil
General Refuse*	1.32 m <sup>3</sup>

<sup>\*</sup> Included the site office

#### 5 Summary of Deficiencies and Remedial Actions

There was no deficiency noted from the site inspections in June 2009.

#### 6 Summary of Complaints and Remedial Actions

There was no EPD visit in June 2009 and no abatement notice nor prosecution was raised by EPD.

No Complaint was received in June 2009. In the event of complaints, the procedure for handling of the complaints is detailed in the EM&A Manual.

#### 7 Summary of Summons and Prosecutions

No notification of summons and prosecutions occurred in June 2009.

#### 8 Monthly Environmental Auditing for the Coming Months

The planned activities for July 2009 - September 2009 as regards E&M equipment are mainly the Installation and Testing & Commissioning (if required) for i) Filter Press at New Press House Extension, ii) Sludge Conditioning Tank Nos.3 & 4, iii) Ferric Chloride Storage Tank at Bunded Area, iv) Deodourizers at Inlet Work & Sludge Holding Tanks, v) Waste Gas Burner;

Defects for SAS Thickening System in SAS Consolidation House (Section 5) and BR5 unit & associated equipment (Section 6, 7 & 8) are scheduled to rectify.

The planned activities for the coming three months (July 2009 – September 2009) as regards E&M equipment are to carry out installation, testing and commissioning for the following system/area:-

- Filter Press at New Press House Extension
- Sludge Conditioning Tank Nos. 3 and 4
- Ferric Chloride Storage Tank at Bunded Area
- Deodourizers at Inlet Work & Sludge Holding Tanks
- Waste Gas Burner

The anticipated environmental issues for July 2009 - September 2009 will be as follows:-

- Filter Press at New Press House Extension
  - The anticipated environmental issues will be related to:-
    - the waste disposal from the E&M equipment installation.

- Sludge Conditioning Tank Nos. 3 and 4
  - The anticipated environmental issues will be related to:-
    - the waste disposal from the E&M equipment installation.
- Ferric Chloride Storage Tank at Bunded Area
  - The anticipated environmental issues will be related to:-
    - waste disposal from the E&M equipment installation.
- Deodourizers at Inlet Work & Sludge Holding Tanks
  - The anticipated environmental issues will be related to:-
    - waste disposal from the E&M equipment installation.
- Waste Gas Burner
  - The anticipated environmental issues will be related to:-
    - waste disposal from the E&M equipment installation.

#### 9 Conclusions and Comments

The required weekly site inspections have been conducted. No deficiency was noted during the reporting month.

CONTROLLED DOCUMENT Doc. No.: RPT:MRPTNo.37/RevA/81869

## Appendix 1

Contact Information of Key Environmental Personnel

## Contact Information for Key Personnel

Name	Title	Telephone	Fax
Mr. K. K. Cheung (DSD)	Engineer's Representative	2594-7338	2827-8532
Mr. Ben Yuen (BML)	Deputy Site Agent 2671-2350		2671-2351
Mr. Kenneth Leung (BML)	Deputy Site Agent	2671-2350	2671-2351
Mr. S. M. Ho (BML)	Site Waste Manager/ Co-ordinator	2671-2350	2671-2351
Mr. Stanley Lau (KEL)	ET Leader	2612-2817	2614-7012
Mr. Tony Yeung (KEL)	ET Site Inspector	2612-2817	2614-7012
Mr. Y. T. Tang (CH2M)	The Independent Environmental Checker	3105-8686	2891-0305

## Appendix 2

Sensitive Receivers,

Location of Monitoring and Control Station,

Action and Limited Levels

and

Event/Action Plan

. . .

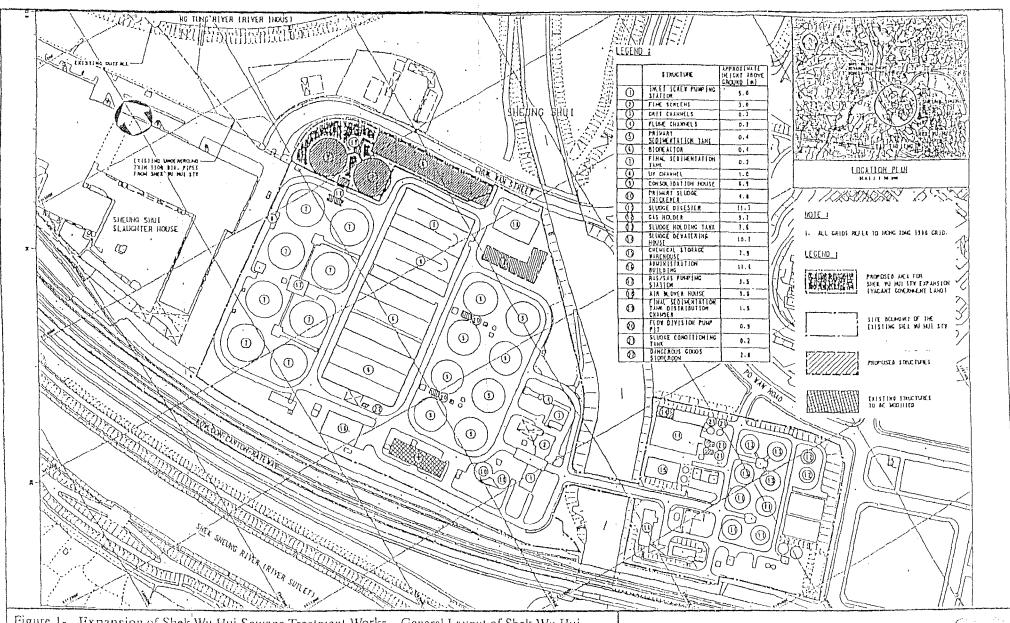


Figure 1- Expansion of Shek Wu Hui Sewage Treatment Works - General Layout of Shek Wu Hui Sewage Treatment Works Upon Project Completion


圖一 - 石湖塊污水處理廠擴建工程 - 石湖塊污水處理廠於工程完成後的平面圖


Environmental Permit No.: EP-218/2005

環境許可證編號: EP-218/2005



CONTRACTOR OF

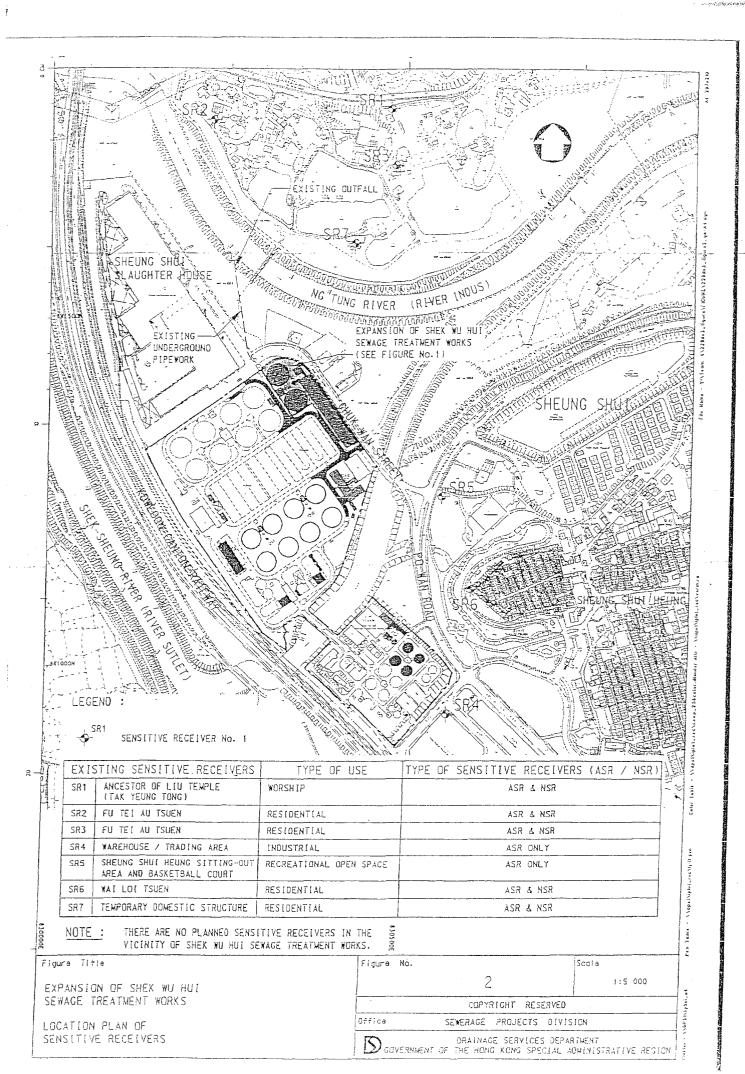

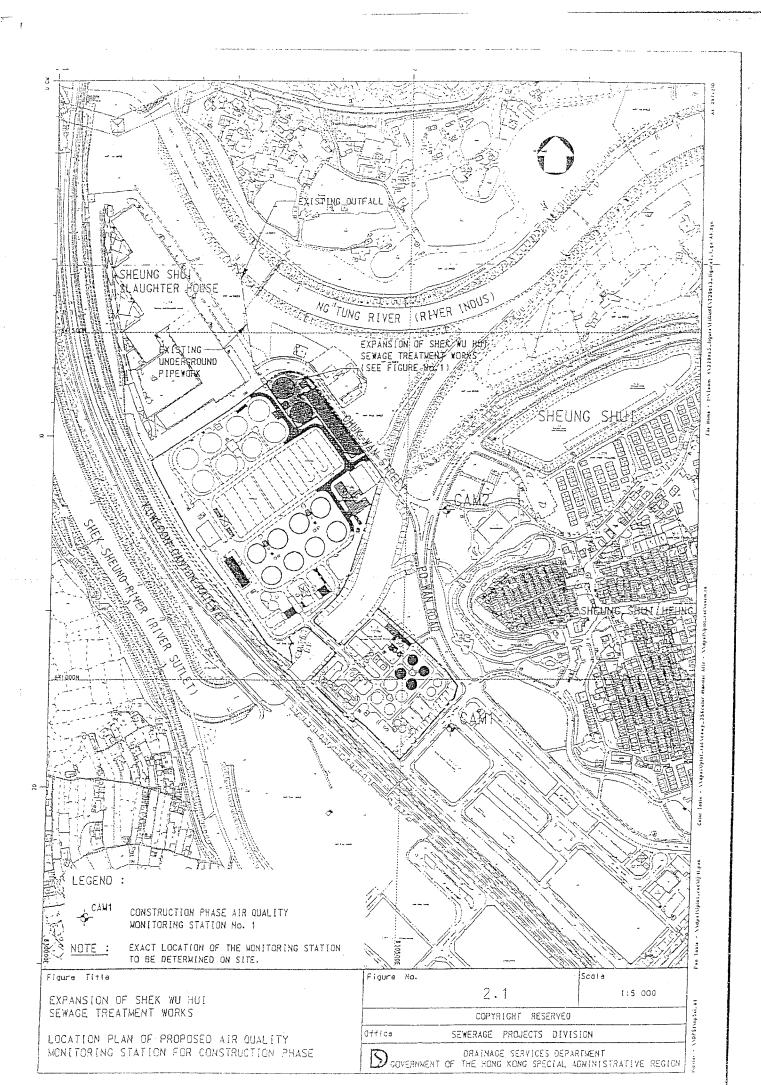

olfactory senses to detect any odour.

- 2.6.9 The observer should bring along a log book to record the findings. The log book should be kept in the plant office where it can be inspected when necessary. The findings should include the following:
  - the prevailing weather condition;
  - the wind direction;
  - location where odour is spotted;
  - possible source of odour;
  - perceived intensity of the odour; and
  - duration of odour.
- 2.6.10 The perceived intensity is to be divided into 5 levels which are ranked in the descending order as follows:
  - Extreme
  - Strong
  - Moderate
  - Slight
  - Not detectable

#### 2.7 Compliance Assessment

→ 2.7.1 Action and Limit (A/L) levels that provide an appropriate framework for the interpretation of monitoring results have to be agreed between ET, IEC, EPD and the Engineer before commencement of the air quality monitoring. The air quality monitoring data shall be checked against the agreed A/L levels. Recommended A/L levels are listed in Table 2.5.

Table 2.5 Proposed Action and Limit Levels for Impact Monitoring

Parameter	Action Level <sup>(1)</sup>	Limit Level
TSP	• BL $\leq$ 200 g m <sup>-3</sup> , AL = (BL * 1.3 + LL)/2	260 g m <sup>-3</sup>
(24 hour average)	• BL > 200 g m <sup>-1</sup> , AL = LL	
TSP	• BL $\leq$ 384 g m <sup>3</sup> , AL = (BL * 1.3 + LL)/2	500 g m <sup>-3</sup>
(1 hour average)	• BL > 384 g m <sup>-3</sup> , AL = LL	
H₂S (at ASRs only)	<ul> <li>BL ≤ 1.92 ppb, AL = (BL * 1.3 + LL)/2</li> <li>BL &gt; 1.92 ppb, AL = LL</li> </ul>	2.5 ppb
incidence of Any incidence of odour complaint received odour complaints through the Odour Complaint Register		Two or more complaints through the Odour Complaint Register within three months


<sup>(1)</sup> BL = Baseline level, AL = Action level, LL = Limit level.

#### Event and Action Plan (EAP) for Air Quality

2.7.2 The EAP is based on the prescription of procedures and actions associated with the measurement of certain defined levels of air pollution recorded by the environmental monitoring process and the agreed A/L levels. In case TSP A/L level exceedances occur, the ET, the IEC, the Engineer and the Contractor shall observe the relevant actions of the respective EAP listed in Tables 2.6 whereas relevant sections in DSD shall be responsible for the implementation of the EAP as listed in Table 2.7 in the event of odour exceedance/complaint for construction and operational phase respectively.

Table 2.6 Event/Action Plan for Air Quality Monitoring (Construction Phase)

	EVENT ACTION ACTION ACTION				
EACIAT	ET	IEC	ER	CONTRACTOR	
ACTION LEVEL	**************************************				
Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding.	Check monitoring data submitted by ET;     Check Contractor's working method.	1. Notify Contractor.	t. Rectify any unacceptable practice;  2. Amend working methods if appropriate.	
2. Exceedance for two or more consecutive samples	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and ER; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	Confirm receipt of notification of exceedance in writing;     Notify Contractor;     Ensure remedial measures properly implemented.	1. Submit proposals for remedial actions to IEC within three working days of nonfication; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.	
Exceedance for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform Contractor, IEC, ER, and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 6. If exceedance stops, cease additional monitoring.	Check monitoring data submitted by ET;     Check Contractor's working method;     Discuss with ET and Contractor on possible remedial measures;     Advise the ER on the effectiveness of the proposed remedial measures;     Supervise implementation of remedial measures.	Confirm receipt of notification of exceedance in writing;     Notify Contractor;     Ensure remedial measures properly implemented.	exceedance; 2. Submit proposals for renxedial actions to IEC	
2. Exceedance for two or more consecutive samples	1. Notify IEC, ER, Contractor and EPD; 2. Identify source, investigate the causes of exceedance and propose remedial measures; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Amange meeting with IEC and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.		exceedance in writing; 2. Notify Contractor; 3. In consolidation with the IEC, agree with the Contractor on the remedial invasures to	execedance;  Submit proposals for remedial actions to His within three working days of norification;  Implement the agreed proposals;  Resubmit proposals if problem still not undecontrol;  Stop the relevant portion of works as determine by the ER until the exceedance is abated.	

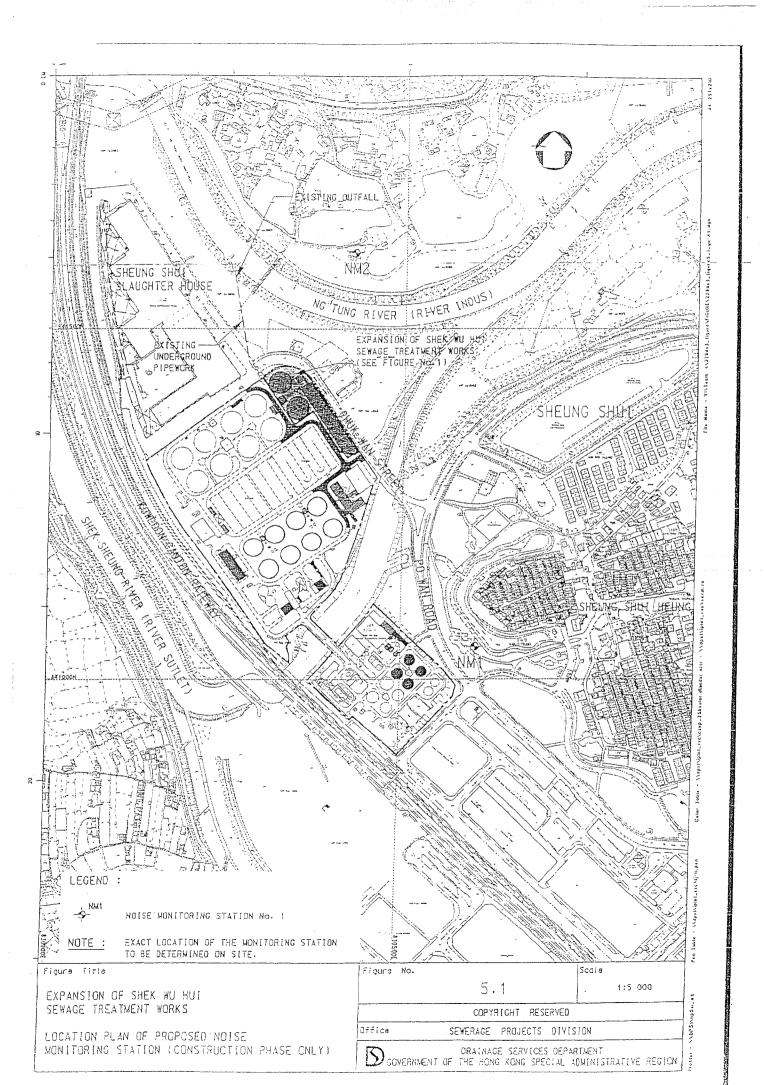

#### 5.6 Impact Monitoring for Construction Noise

- 5.6.1 Noise monitoring shall be carried out at all designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:
  - one set of measurements between 0700 and 1900 hours on normal weekdays.
- 5.6.2 If construction works are extended to include works during the hours of 1900 0700. Applicable permits under NCO shall be obtained by the Contractor.
- 5.6.3 In case of non-compliance with the construction noise criteria, more frequent monitoring, as specified in the Action Plan in Table 5.3, shall be carried out. This additional monitoring shall be continued until the recorded noise levels are rectified or proved to be irrelevant to the construction activities.
- 5.6.4 Before commencement of impact monitoring, the ET Leader shall inform IEC of the impact monitoring programme such that the IEC can conduct an on-site audit to ensure the accuracy of the monitoring results.

#### 5.7 Event and Action Plan (EAP) for Construction Noise

5.7.1 The Action and Limit levels for construction noise are defined in Table 5.2. Shall non-compliance of the criteria occur, action in accordance with the Action Plan in Table 5.3-shall be implemented.


Table 5.2 Action and Limit Levels for Construction Noise

Time Period	Action Level	Limit Level
0700 – 1900 hours	When one documented	75 dB(A)
on normal weekdays	complaint is received	

Table 5.3	Event/Action Plan for Construction Nois	2		
EVENT		ACTIO	N	
	ET	IEC:	ER	CONTRACTOR
Action Level	<ol> <li>Notify IEC and ER;</li> <li>Carry out investigation;</li> <li>Report the results of investigation to the IEC, ER and Contractor;</li> <li>Discuss with the Contractor and formulate remedial measures;</li> <li>Increase monitoring frequency to check mitigation effectiveness.</li> </ol>	<ol> <li>Review the analysed results submitted by the ET;</li> <li>Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	<ol> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Require Contractor to propose remedial measures for the analysed noise problem;</li> <li>Ensure remedial measures are properly implemented.</li> </ol>	1. Submit noise mitigation proposals to IEC; 2. Implement noise mitigation proposals.
Limit Level	<ol> <li>Identify source;</li> <li>Inform IEC, ER, EPD and Contractor;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency to check mitigation effectiveness;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Inform IEC, ER and EPD the causes and actions taken for the exceedances;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> </ol>	<ol> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	1. Confirm receipt of notification of failure in writing;  2. Notify Contractor;  3. Require Contractor to propose remedial measures for the analysed noise problem;  4. Ensure remedial measures properly implemented;  5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	<ol> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control;</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated.</li> </ol>

Appendix 3

Construction Programme

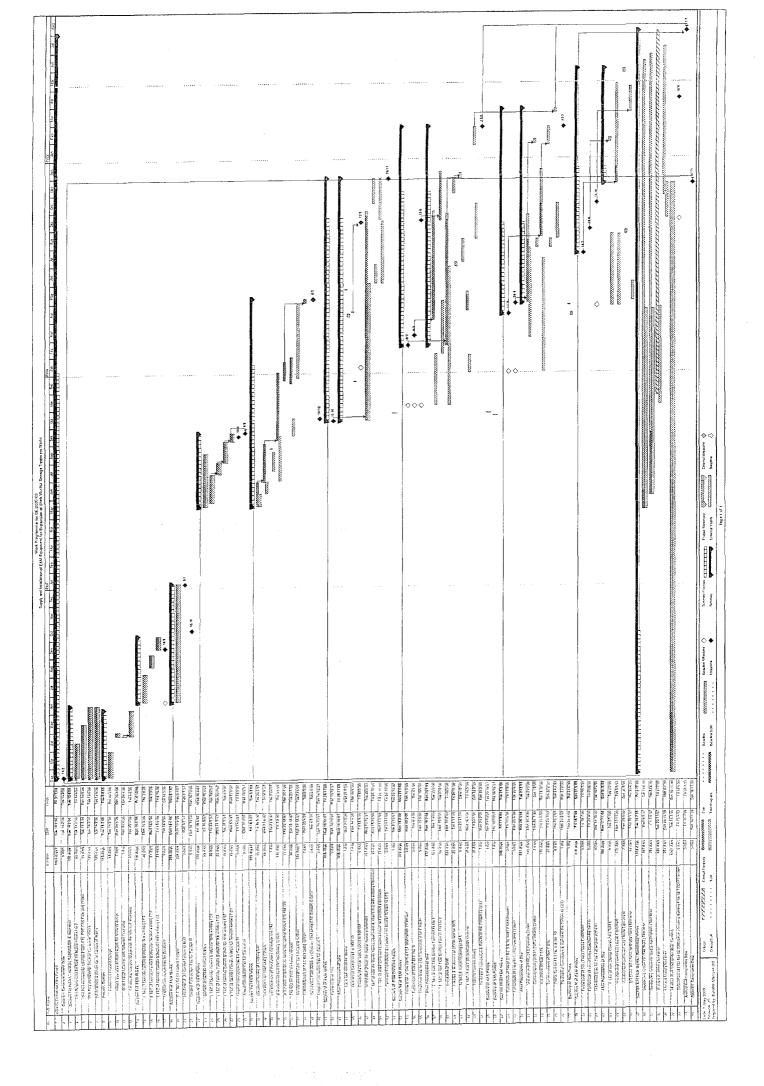

## Appendix 4

Environmental Requirements and Implementation Status

#### APPENDIX B IMPLEMENTATION SCHEDULE OF MITIGATION MEASURES

#### Implementation Schedule for Air Quality Control

PP Ref <sup>#</sup>	Environmental Protection Measures	Location / Timing	Implementation Agent	Implementation Stages *			Relevant Legislation &
TCI				D	С	О	Guidelines
Annex 1 S1.7.1	Dust mitigation measures stipulated in the Air Pollution Control (Construction Dust) Regulation shall be incorporated to control dust emission from the Site. Notice shall be given to the authority prior to commencement of works.	Work sites / during construction period	Contractor	Salar a salar	7		Air Pollution Control (Construction Dust) Regulation
Annex 1 S1.7.6 – S1.7.9	Exposed area of inlet screw pumping station excluding its inlet chamber; and sludge holding tanks should be covered, with the foul air drawn through deodourizers and discharged after treatment. Exposed area of grit channels, flume channels and effluent launder channels of primary sedimentation tanks should be covered.	SWHSTW / during design and operation stage	DSD	7			

# The section number in the Project Profile for Expansion of Shek Wu Hui Sewage Treatment Works (Application No. DIR-121/2005)

<sup>\*</sup> D = Design, C = Construction and O = Operation

#### Implementation Schedule for Water Quality Control

PP Ref <sup>#</sup>	Environmental Protection Measures Location / Timing Implementation Agent		Implementation Agent	Implementation Stages *			Relevant Legislation &
Kei		$\alpha$	С	o	Guidelines		
Annex 2 S2.4.4	The practices outlined in Practice Note for Professional Persons on Construction Site Drainage, Professional Persons Environmental Protection Department, 1994 (ProPECC PN 1/94) including the use of sediment traps, wheel washing facilities for vehicles leaving the site, adequate maintenance of drainage systems to prevent flooding and overflow, sewage collection and treatment, and comprehensive waste management (collection, handling, transportation, disposal) procedures should be adopted to minimize the potential water quality impact from construction site runoff and various construction activities.	During the construction period	Contractor		1		ProPECC PN 1/94; WPCO, Waste Disposal Ordinance

PP Ref <sup>#</sup>	Environmental Protection Measures	Location / Timing	Implementation Agent		ementa tages		Relevant Legislation &
Annay 2		1 mmg		a	c	llo	Guidelines
Annex 2 ·· S2.4.4	<ul> <li>At the start of site establishment, perimeter cut-off drains to direct off-site water around the site should be constructed and internal drainage works and erosion and sedimentation control facilities implemented. Channels, earth bunds or sand bag barriers should be provided on site to direct stormwater to silt removal facilities. The design of the temporary on-site drainage system will be undertaken by the contractor prior to the commencement of construction.</li> <li>The design of efficient silt removal facilities should be based on the guidelines in Appendix A1 of ProPECC PN 1/94, which states that the retention time for silt/sand traps should be 5 minutes under maximum flow conditions. Sizes may vary depending upon the flow rate, but for a flow rate of 0.1m³s⁻¹ a sedimentation basin of 30m³ would be required and for a flow rate of 0.5m³s⁻¹ the basin</li> </ul>	aanatmiatia	Contractor	Ü	C		ProPECC PN 1/94; WPCO, Waste Disposal Ordinance
	would be 130m. The detailed design of the sand/silt traps will be undertaken by the contractor prior to the commencement of construction.  Ideally, construction works should be programmed to minimize surface excavation works during the rainy season (April to September). All exposed earth areas should be compacted and vegetated as soon as possible after earthworks have been completed, or alternatively, within 14 days of cessation of earthworks where practicable. If excavation of soil cannot be avoided during the rainy season, or at any time of year when	- - - - -					
	rainstorms are likely, exposed slope surfaces should be covered by tarpaulin or other means.  • The overall slope of the site should be kept to a minimum to reduce the erosive potential of surface water flows, and all trafficked areas and access roads protected by coarse stone ballast. An additional advantage accruing from the use of crushed stone is the positive traction gained during prolonged periods of inclement weather and the reduction of surface sheet flows.						

PP Ref <sup>#</sup>	Environmental Protection Measures	Location /	Implementation Agent	Implementation Stages *			Relevant Legislation &
Rei	·	Timing		D	D C O	Guidelines	
Annex 2 S2.4.4	<ul> <li>Construction Runoff and Drainage (Cont'd)</li> <li>All drainage facilities and erosion and sediment control structures should be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rainstorms. Deposited silt and grit should be removed regularly and disposed of by spreading evenly over stable, vegetated areas.</li> <li>Measures should be taken to minimize the ingress of site drainage into excavations. If the excavation of trenches in wet periods is necessary, they should be dug and backfilled in short sections wherever practicable. Water pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.</li> <li>Open stockpiles of construction materials (for example, aggregates, sand and fill material) of more than 50m³ should be covered with tarpaulin or similar fabric during rainstorms. Measures should be taken to prevent the washing away of construction materials, soil, silt or debris into any drainage system.</li> <li>Manholes (including newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the drainage system and storm runoff being directed into foul sewers.</li> <li>Precautions to be taken at any time of year when rainstorms are likely, actions to be taken when a rainstorm is imminent or forecasted, and actions to be taken during or after rainstorms are summarized in Appendix A2 of ProPECC PN 1/94. Particular attention should be paid to the control of silty surface runoff during storms events, especially for areas located near steep slopes.</li> </ul>	construction	Contractor		7		ProPECC PN 1/94; WPCO, Waste Disposal Ordinance

PP Ref <sup>#</sup>	Environmental Protection Measures	Location /	Implementation Agent	Implementation Stages *			Relevant Legislation &	
ACCI		Timing		D	C	o	Guidelines	
Annex 2 S2.4.4	<ul> <li>Construction Runoff and Drainage (Cont'd)</li> <li>All vehicles and plant should be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and sited wheel washing bay should be provided at every site exits and washwater should have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access roadrleading to, and exiting from, the wheelwash bay to the public road should be paved with sufficient backfill toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains.</li> <li>On-site drainage system should be equipped with oil interceptors to separate oil/fuel from contaminated storm water.</li> </ul>	Work site / During the construction period	Contractor		7		ProPECC PN 1/94; WPCO, Waste Disposal Ordinance	
Annex 2 S2.4.4	General Construction Activities  Construction solid waste, debris and rubbish on site should be collected, handled and disposed of properly to avoid water quality impacts.	Work site / During the construction period	Contractor		1		ProPECC PN 1/94; WPCO, Waste Disposal Ordinance	
	• All fuel tanks and storage areas should be provided with locks and sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank to prevent spilled fuel oils from reaching water sensitive receivers nearly.							
Annex 2 S2.4.4	Sewage from Construction Workforce  • Sewage from construction workforce should be handled by portable chemical toilets or sewage holding tanks with the sewage regularly collected by a reputable sewage collector for disposal at, for example, SWHSTW. Sewage from on-site toilets should be diverted to and stored within sewage holding tanks for later disposal.	Work site / During the construction period	Contractor		1		ProPECC PN 1/94; WPCO, Waste Disposal Ordinance	
Annex 2 S2.5.3 – S2.5.11	The implementation programme of the village sewerage should be monitored to achieve the target sewerage connection to communal sewers.	SWHSTW/ During the operation period	DSD			N I	ProPECC PN 1/94; WPCO, Waste Disposal Ordinance	

PP.	Environmental Protection Measures	Location /	Implementation Agent	Implementation Stages *			Relevant - Legislation &
Ref"		Timing		a	С	O	Guidelines
Annex 2 S2.5.12	Standby equipment will provide further safeguard on proper functioning of all key treatment facilities e.g. standby air blowers to ensure adequate air supply for the biological treatment process and standby pumps to prevent any overflow of sewage due to mechanical failure of pumps. In the remote case that untreated effluent is discharged, an emergency contingency plan has been formulated to minimize the impact of emergency discharges and facilitate subsequent management of emergency. If there is a power failure, the plant manager will start up the emergency generator to provide electricity supplies for the pumps and regularly monitor the quality of effluent discharge.	SWHSTW/ During the design and operation period	DSD			7	ProPECC PN 1/94; WPCO, Waste Disposal Ordinance
Annex 2 S2.7.2	Routine monitoring of the effluent quality from the SWHSTW should be conducted in order to satisfy the conditions of the WPCO discharge licence.	SWHSTW/ During the operation period	DSD			₩ :	ProPECC PN 1/94; WPCO, Waste Disposal Ordinance

# The section number in the Project Profile for Expansion of Shek Wu Hui Sewage Treatment Works (Application No. DIR-121/2005)

\* D = Design, C = Construction and O = Operation

### Implementation Schedule for Waste Management

PP Ref <sup>#</sup>	Environmental Protection Measures	Location / Timing	Implementation Agent`	Implementation Stages *			Relevant Legislation &
Rei				$\mathbf{a}$	С	o	Guidelines
Annex 3 S3.5.1	<ul> <li>Waste Reduction Measures at Planning and Design Stage</li> <li>The levels of structures should be designed such that excavation could be minimized as far as practicable.</li> <li>Excavated materials generated from construction works to be re-used on-site as far as practicable to reduce off-site disposal.</li> <li>Control measures recommended under the prevailing ETWB circulars should be strictly followed to ensure proper management of the C&amp;D materials with an aim to minimize the generation of C&amp;D material and maximize the use of inert C&amp;D material.</li> </ul>		DSD	7			ProPECC PN 1/94; WPCO, Waste Disposal Ordinance

PP	Environmental Protection Measures	Location / Imp	Implementation Agent	Implementation Stages *			Relevant Legislation &
Ref#		Timing		а	С	O	Guidelines
Annex 3 S3.5.1	<ul> <li>Waste Reduction Measures at Construction Stage</li> <li>Measures recommended in the ETWB TCW No. 15/2003 should be followed to require the contractor to prepare and implement an enhanced Waste Management Plan (WMP) to encourage on-site sorting of C&amp;D materials and to minimize their generation during the course of construction.</li> <li>For the demolition works, the contractor shall submit a method statement for the works as part of the WMP. The Contractor shall include in the method statement the sequence of demolition and the work programme to facilitate effective recovery of reusable and/or recyclable portions of the C&amp;D materials at the earliest stage, so as to minimise the need for subsequent sorting.</li> <li>Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal.</li> <li>Separate labelled bins shall be provided to segregate aluminium cans from other general refuse generated by the work force, and to encourage collection of by individual collectors.</li> <li>Any unused chemicals or those with remaining functional capacity shall be recycled.</li> <li>Maximising the use of reusable steel formwork to reduce the amount of C&amp;D material.</li> <li>Prior to disposal of C&amp;D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill.</li> <li>Proper storage and site practices to minimise the potential for damage or contamination of construction materials.</li> <li>Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> <li>Minimize over ordering of concrete, mortars and cement grout by doing careful check before ordering.</li> </ul>		Contractor				ProPECC PN 1/94; WPCO, Waste Disposal Ordinance

PP Ref <sup>#</sup>	Environmental Protection Measures	Location /	Implementation Agent	Implementation Stages *			Relevant Legislation &	
Kei		Timing		a	С	o	Guidelines	
Annex 3 S3.5.2 – S3.5.5	<ul> <li>Good Site Practices</li> <li>nomination of approved personnel, such as a site manager, to be responsible for good site practices, and making arrangements for collection of all wastes generated at the site and effective disposal to an appropriate facility.</li> <li>training of site personnel in proper waste management and chemical waste handling procedures;</li> <li>Provision of sufficient waste disposal points and regular collection for disposal;</li> <li>appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;</li> <li>regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors;</li> <li>a Waste Management Plan should be prepared and should be submitted to the Engineer for approval; and</li> <li>a recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed.</li> <li>In order to monitor the disposal of C&amp;D material at landfills and public filling facilities, as appropriate, and to control fly tipping, a trip-ticket system should be included as one of the contractual requirements to be implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. The measures recommended in ETWB TCW No. 31/2004 should be followed.</li> </ul>	period	Contractor		7		ProPECC PN 1/94; WPCO, Waste Disposal Ordinance	

PP Ref <sup>#</sup>	Environmental Protection Measures	Location /	Implementation Agent	Implementation Stages *			Relevant Legislation &
IXC1		Timing		D	C	O	Guidelines
Annex 3 S 3.5.6	General Refuse  • General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material;	Work sites / During the construction period	Contractor		7		EIAO-TM and Noise Control Ordinance
Annex 3 S 3.5.7	<ul> <li>Construction and Demolition Material</li> <li>The C&amp;D material generated from the site formation and demolition works should be sorted on-site into inert C&amp;D material (that is, public fill) and C&amp;D waste. In order to minimise the impact resulting from collection and transportation of C&amp;D material for off-site disposal, the excavated material comprising fill material should be reused on-site as backfilling material as far as practicable. C&amp;D waste, such as wood, plastic, steel and other metals should be reused or recycled and, as a last resort, disposed of to landfill. A suitable area should be designated within the site for temporary stockpiling of C&amp;D material and to facilitate the sorting process.</li> </ul>		Contractor				EIAO-TM and Noise Control Ordinance

PP	Environmental Protection Measures	Location / Timing	Implementation Agent	, -	menta tages *	1	Relevant Legislation & Guidelines
Ref*				р	С	O	
Annex 3 S 3.5.8	<ul> <li>When chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the requirements stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used. Appropriate labels should be securely attached on each chemical waste container indicating the chemical characteristics of the chemical waste, such as explosives, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed waste collector to transport and dispose of the chemical wastes in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.</li> </ul>	Work sites / During the construction period	Contractor		7		EIAO-TM and Noise Control Ordinance

<sup>#</sup> The section number in the Project Profile for Expansion of Shek Wu Hui Sewage Treatment Works (Application No. DIR-121/2005)
\* D = Design, C = Construction and O = Operation

#### Implementation Schedule for Noise Control

PP.	Environmental Protection Measures	Location /	Implementation Agent	Implementation Stages *			Legislation &	
Ret#		Timing		a	C	o	Guidelines	
Annex 4 S4.7.1	Use of quiet PME	Work sites / During the construction period	Contractor		1	;	EIAO-TM and Noise Control Ordinance	
Annex 4 S4.7.3	<ul> <li>Good Site Practice</li> <li>Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction phase;</li> <li>Silencers or mufflers on construction equipment should be utilised, if found necessary, to further reduce noise, and should be properly maintained during the construction phase;</li> <li>Mobile plant should be sited as far away from NSRs as possible;</li> <li>Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum;</li> <li>Plant known to emit noise strongly in one direction, should, where possible, be orientated so that the noise is directed away from nearby NSRs; and</li> <li>Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.</li> </ul>		Contractor				EIAO-TM and Noise Control Ordinance	


# The section number in the Project Profile for Expansion of Shek Wu Hui Sewage Treatment Works (Application No. DIR-121/2005)
\* D = Design, C = Construction and O = Operation

Site layout plan

and

Site Inspection Checklists

### Shek Wu Hui STW – Expansion E&M Works EM&A Site Inspection – June 2009 Site Layout

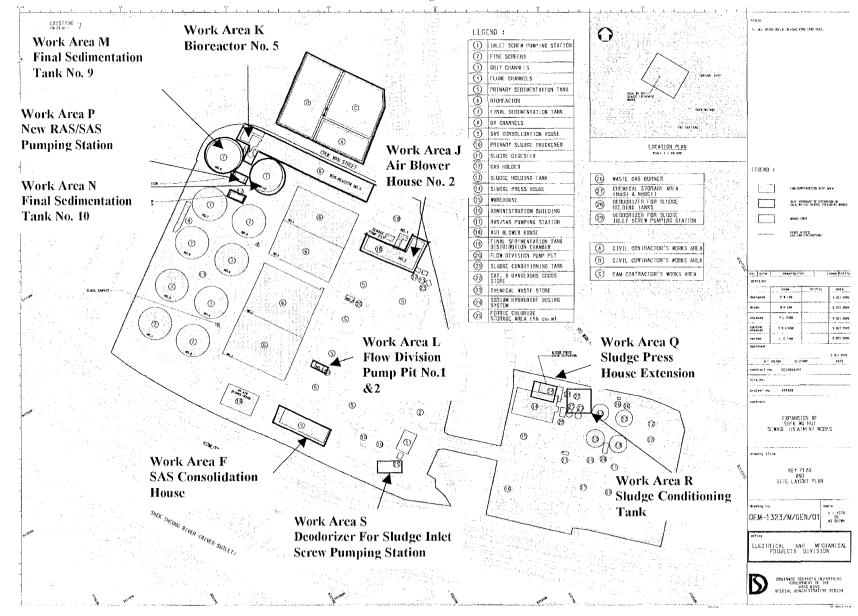

Inspection Date: 4th June 2007			Time: <u>৩৭</u> ৫			0-1030		
DSD	ted By: M.H. Yaen sentative: <u>K.K. Chang</u>	M. K. Law			Contrac sentativ		SM, Ho ,	Kennyth Leun Fonkse Chan
	nmental Inspector: <u>Tany Ye</u>	unij.						
Weath	er		·					
Conditio		Fine Overo	ast	 Drizzle	R	ain	Storm	Hazy
Temper	ature 27°C	Humid	ity	Po o	%			
Wind	Calm I	Light Breez	] e \$	Strong		Directior	תונון ו	
Ref.	Brief Description	0.00		tivity C	omplia	Action Required/ Responsible Party		
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Respons	ible Party <sup>e</sup> "
Air Qu	ıality - Dust							
1	Water spray	6,5,6,6,10,0, 0,6,0,4;			1			
2	Cover debris				1/			
3	Wet & cover stockpile				V			
4	Skip hoist				V			
5	Vehicle washing				V			
6	Clear of dusty material				1			
7	Water spray on road				1			
8	Cement bags				1			
9	Dusty material				V			
10	Cover belt conveyor				V			
Water	Quality							
11	Storm drains	F, 5, K, L, M, M			V			
12	Sand/silt removal facilities	ο, ρ.ω, ρ.:			V			
13	Exposed soil surface				V			
14	Rainwater silt removal		V		-			
15	Open stockpiles	No. CELL COLLEGE			V			
16	Groundwater silt	10 D. C.		1	V			

Ref.	Brief Description	Site	Ac	tivity C	Complia	nce	Action Required/
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>
17	Large object	F.J. K.L. M.N. O. P.Q. R.S			V		
18	Sewage discharged		2				
19	Fuel/chemical storage		<b>レ</b>				
20	Storage area condition		~				
21	Clean-up actions		V				
Noise	Control						
22	Comply with ordinance	F. T. K.L, M.W.O. P. C. R.S	V				
23	Working equipment & sound-reducing measures				1		
24	Equipment condition		اسمرا				
25	Well-maintained plant				V		
26	Intermittent use of machines/plants				V		
27	Noise in one direction				~		
28	Silencers/mufflers				2		
29	Away from NSRs				v		
30	Trial for equipment/sound-reducing measures	<u></u>			V		
Waste 31	Disposal  Construction wastes	F.J.K, L, M,N,	W				
32	Licensed waste collector	0:1,6,8,5			V		
33	Removal of construction wastes		V				
34	Waste storage areas		0				
35	Windblown litter/dust				V		
36	Waste disposal permits				1		
37	Licensed waste disposal facilities		V				
38	Careful design, planning & good site management				V		
39	Bentonite slurries				0		
40	Chemical wastes handling		0				
41	Chemical waste storage						
42	Condition of chemical waste storage area		1				}

Ref.	Brief Description	Site	Ac	tivity C	omplia	псе	Action Required/
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>
43	Disposal of chemical wastes	F, J, K, L, M, N, O, P, Q, RS			V		
44	General refuse						
45	Chemical waste separation		V				
46	Strictly prohibited of refuse burning		U				
47	Environmental Permit and other documents on-site		Ü				
48	Environmental Permit and license displayed		U				
49	Waste records		U				

Sum	mar	I/R	Rema.	rks <sup>(4)</sup>

Installation works of E&M equipment were observed at Sludge Presi House Extension. Arr Blower House No. 2, Studge Conditioning Tank and Desconfor for Inlet Pumping Station.

Particular observation.

(Note: Refer to attached site layout)

#### Signatures

DSD Representative

E&M Contractor Representative

Name:

Environmental Team Leader

Name:

Refer to Site Inspection Checklist Attachment for complete description (Summarized EM&A Manual) of referenced mitigation measure or requirement.

Indicate exact locations as indicated (by code) on the attached site layout.

Note actions/plans and responsible party regarding any non-compliance in this column.

To be filled out by the environmental team.

Inspec	tion Date: 🏻 🏋 ரி	we loof		Time:	1430	- 1530		
DSD	ited By: Իւթ, Վա sentative: <u>k.k. Ո</u> ւ	en H.K. Ista		E&M Con Represer		S.M. Ho Y.H. Hong	, Leaneth Lea Frankie Cha	
	nmental Inspector: <u>Tony</u>	Yeung						
Weath								
Condition	on Sunny	Fine Over	cast [	 Drizzle	Rain	Storm	Hazy	
Temper	ature 28 °C	Humic	lity	<b>3</b> 0 %				
Wind	Calm	Light Breez	] [ ze S	itrong	Directio	n SW		
Ref.	Brief Description	Oite	Activi			pliance		Required/
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No N	/A Unk	Responsi	ole Party <sup>(3)</sup>	
Air Qu	ıality - Dust							
1	Water spray	F.D.K.L.M.N., O.P.O. F.S		L	7			
2	Cover debris			v				
3	Wet & cover stockpile			2				
4	Skip hoist			J				
5	Vehicle washing	Manager (C)		اسما				
6	Clear of dusty material			V				
7	Water spray on road			V				
8	Cement bags			V				
9	Dusty material			1				
10	Cover belt conveyor							
Water (	Quality							
11	Storm drains	F, S, K, L, M, W, O, P, Q, R, S		V				
12	Sand/silt removal facilities			V				
13	Exposed soil surface			V				
14	Rainwater silt removal		U					
15	Open stockpiles			1/				
16	Groundwater silt removal			1,/				

Ref.		Site		tivity (	Complia	nce	Action Required/
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>
17	Large object	F, J, K, L, M, N, O, P, E, R, S			1		
18	Sewage discharged		100				
19	Fuel/chemical storage		1				
20	Storage area condition		1				
21	Clean-up actions						
Noise	: Control						
22	Comply with ordinance	F, T, K, L, M, W O, P, Q, P, S					
23	Working equipment & sound-reducing measures	0717 00 7 10 10			J		
24	Equipment condition		1				
25	Well-maintained plant	75.			V		
26	Intermittent use of machines/plants				~		
27	Noise in one direction				1		
28	Silencers/mufflers				V		
29	Away from NSRs				V		
30	Trial for equipment/sound-reducing measures				V		
Waste	Disposal	See on 5 A					
31	Construction wastes	FITHLIM, NO.P.R.R.S					
32	Licensed waste collector				1		
33	Removal of construction wastes	Property (p. mookygy)					
34	Waste storage areas	Approprie	1				
35	Windblown litter/dust				V		
36	Waste disposal permits	40.00			1		
37	Licensed waste disposal facilities		V				
38	Careful design, planning & good site management				V		
39	Bentonite slurries				V		
40	Chemical wastes handling		U				
41	Chemical waste storage		1				
42	Condition of chemical waste storage area						

Ref.	Brief Description	Site	Ac	tivity C	omplia	Action Required/	
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>
43	Disposal of chemical wastes	F, 5, K, L, M, N, O, B Q, RS			V		
44	General refuse		V				
45	Chemical waste separation						
46	Strictly prohibited of refuse burning		/				
47	Environmental Permit and other documents on-site						
48	Environmental Permit and license displayed		V				
49	Waste records		1				

_	٠.		(4)
Summary	//	Remai	rks(*)

Installation works of E&M equipment were observed at Shidge Pless Youre Extension. Am Blower House No. 2, Shidge Conditioning Tank and Peodorizen for Inlet pumping statem.

No particular observation.

Signatures

DSD Representative

E&M Contractor Representative

Name: M. H. YUEN

Name: H. SIK MING

Environmental Team Leader

- Refer to Site Inspection Checklist Attachment for complete description (Summarized EM&A Manual) of referenced mitigation measure or requirement.
- [2] Indicate exact locations as indicated (by code) on the attached site layout.
- Note actions/plans and responsible party regarding any non-compliance in this column.
- <sup>(4)</sup> To be filled out by the environmental team.

Name:

Inspec	tion Date: <u>16 <sup>th</sup> Tun</u>	2009		Time:	_	043	0-1030
DSD	ted By: リリー・パー sentative: <u>ド.ド. Ch</u>	nen eung 14.K. Lan		E&M Co			S. M. Ho T. Kenneth leang Y. H. Hong, Eventie Chan
	nmental Inspector: <u>Tony</u>	Yeuny					
Weath		3/	/***				
Conditio	on	Fine Overc	ast	 Drizzle	R	ain	Storm Hazy
Temper	ature ZŸ °C	Humid	ity	°,0 %			
Wind	Calm	Light Breez	re :	Strong		Direction	n [\$/w]
Ref.	Brief Description	Site Location <sup>(2)</sup>		tivity Co			Action Required/ Responsible Party <sup>(3)</sup>
110.	of Mitigation	Location	Yes	No	N/A	Unk	responsible rurty
Air Qı	ıality - Dust						
1	Water spray	F, J, K, L, M, N O, F, Q, R, S			√		
2	Cover debris				V		
3	Wet & cover stockpile				V		
4	Skip hoist				/		
5	Vehicle washing				<b>√</b>		
6	Clear of dusty material						
7	Water spray on road				V		
8	Cement bags						
9	Dusty material						
10	Cover belt conveyor				V V		
Water	Quality						
11	Storm drains	F. J.K. L.M. N.O.					
12	Sand/silt removal facilities	P.Q.R.S			<u>بر</u> س		
13	Exposed soil surface			1			
14	Rainwater silt removal						
15	Open stockpiles				L		
16	Groundwater silt removal						

Ref.	Brief Description	Site	Act	ivity C	omplia	Action Required/	
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>
17	Large object	F, 5, K, L, M, N, O, P, Q, F, S			V		
18	Sewage discharged	The second of th	1				
19	Fuel/chemical storage						
20	Storage area condition	OTTO CONTRACTOR OF STATE OF ST	1				
21	Clean-up actions		1				
Noise	Control						
22	Comply with ordinance	F.J.K, L, M, N, C, P.Q.R.S	1				
23	Working equipment & sound-reducing measures				y		
24	Equipment condition		1				
25	Well-maintained plant	Table to the state of the state			S		
26	Intermittent use of machines/plants	- Committee of the comm			V		
27	Noise in one direction				1/		
28	Silencers/mufflers				1/		
29	Away from NSRs				V		
30	Trial for equipment/sound-reducing measures				V		
Macto	Disposal					<u> </u>	
<u></u> .	<u>,                                      </u>	+ ··· · · · · · · · · · · · · · · · · ·					
31	Construction wastes	F, J, K, L, 14, W, L, C, F, Q, R, S	V				
32	Licensed waste collector				V		
33	Removal of construction wastes		(/				
34	Waste storage areas		1/				
35	Windblown litter/dust				V		
36	Waste disposal permits				V		
37	Licensed waste disposal facilities	Total and the same of the same	0				
38	Careful design, planning & good site management				V		
39	Bentonite slurries	Towns of the Control			1/		
40	Chemical wastes handling		1				
41	Chemical waste storage		V				
42	Condition of chemical waste storage area		<b>1</b>				

Ref.	Brief Description	Site	Ac	tivity (	Complia	Action Required/	
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>
43	Disposal of chemical wastes	F.J.K.L.M.N., O. P.Q.R.S			/		
44	General refuse		1				
45	Chemical waste separation		V				
46	Strictly prohibited of refuse burning		V				
47	Environmental Permit and other documents on-site		V				
48	Environmental Permit and license displayed		1				
49	Waste records	J	J				

Summary	/Rem	arks <sup>(4)</sup>

Installation works of E&M equipment were observed out Sludge Press House Extension, Air Blower House No. 2, Sludge Consists rating Tank and Redorizen for Inlet Station.

No particular observation.

(Note: Refer to attached site layout)

#### Signatures

DSD Representative

E&M Contractor Representative

Name:

IN IL YUEN

ame: Ha c

Environmental Team Leader

Name:

Refer to Site Inspection Checklist Attachment for complete description (Summarized EM&A Manual) of referenced mitigation measure or requirement.

- (2) Indicate exact locations as indicated (by code) on the attached site layout.
- Note actions/plans and responsible party regarding any non-compliance in this column.
- To be filled out by the environmental team.

Inspection Date: 24th June 209			Time:	0930-1030				
Inspect DSD Repres	M. H. Yne	n ng. M.K. Lan		E&M Contrac Representati		S.M. Ho , Kenneth Len Y.H. Hony, Frankie Cha		
	nmental Inspector: <u>lony</u>	Yeang						
Weath	e <i>r</i>							
Conditio	on Sunny	Fine Overc	] [ cast [	rizzle R	ain	Storm Hazy		
Tempera	ature 29 °C	Humid	ity [	70 %				
Wind	Calm	Light Breez	] [ re S	trong	Direction	ا (چۇلار)		
Ref.	Brief Description	Site	Act	ivity Complia	nce	Action Required/		
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No N/A	Unk	Responsible Party <sup>(3)</sup>		
Air Qu	ıality - Dust							
1	Water spray	F.J. K, L, M, D, O, P, W, R, S						
2	Cover debris	1, 19, 1, 5						
3	Wet & cover stockpile			1				
4	Skip hoist							
5	Vehicle washing			V				
6	Clear of dusty material							
7	Water spray on road							
8	Cement bags							
9	Dusty material			V				
10	Cover belt conveyor			V				
Water	Quality							
11	Storm drains	F. S. K. L. M.P. C. P. C. S. S.						
12	Sand/silt removal facilities	1,35,18,3		V				
13	Exposed soil surface			V				
14	Rainwater silt removal							
15	Open stockpiles			V				
16	Groundwater silt							

Ref.	Brief Description of Mitigation	Site Location <sup>(2)</sup>	Ac	tivity C	omplia	Action Required/	
No. <sup>(1)</sup>			Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>
17	Large object	F.J. C. L. M. N. S. B. Q. R. S.			1		
18	Sewage discharged		V				
19	Fuel/chemical storage		1				
20	Storage area condition		1				
21	Clean-up actions	V	1				
Noise	Control						
22	Comply with ordinance	P. J. K. L. M., N.O. P. Q. R. S	./				
23	Working equipment & sound-reducing measures	The state of the s			V		
24	Equipment condition		1				
25	Well-maintained plant	The Committee of the Co			V		
26	Intermittent use of machines/plants				2		
27	Noise in one direction				1		
28	Silencers/mufflers				1		
29	Away from NSRs				1		
30	Trial for equipment/sound-reducing measures	a married and the second			V		
Waste 31	Disposal  Construction wastes	F.T.K, L.M. N.					
	Licensed waste	F. J. K. L. M. N., O. P. Q. R.S.	V				
32	collector	100			1		
33	Removal of construction wastes	dia Wallon and American	1				
34	Waste storage areas	9.73 A.S.	1/				
35	Windblown litter/dust				V		
36	Waste disposal permits				1/		
37	Licensed waste disposal facilities		1				
38	Careful design, planning & good site management				V		
39	Bentonite slurries		T		1/		
40	Chemical wastes handling		~				
41	Chemical waste storage		V				
42	Condition of chemical waste storage area		V		T is a second se		

Ref.	Brief Description	Site	Ac	tivity C	ompliar	Action Required/		
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>	
43	Disposal of chemical wastes	F.J.K.L.M. N.O.P.G.RS			V			
44	General refuse		V					
45	Chemical waste separation		V					
46	Strictly prohibited of refuse burning		V					
47	Environmental Permit and other documents on-site		V					
48	Environmental Permit and license displayed	and the same of th	U					
49	Waste records	$\downarrow$	1					

Summary / Rer	narks <sup>(4)</sup>						
Installation	works	of EAM	equipment	Were	observed	at	
Studie Press	House	Extension	, Am	Blower H	ouse No	2,	Studge
Conditioning	Tank a	ind Devd	or Kr	for Inte	t stalls	m.	
•.1							

No particular observation.

E&M Contractor Representative

Name: #0 57K MING

(Note: Refer to attached site layout)

Signatures

DSD Representative

Name: M. H. YUEN

Environmental Team Leader

Name:

Refer to Site Inspection Checklist Attachment for complete description (Summarized EM&A Manual) of referenced mitigation measure or requirement.

(2) Indicate exact locations as indicated (by code) on the attached site layout.

Inthing Kernel

Note actions/plans and responsible party regarding any non-compliance in this column.

To be filled out by the environmental team.

Insped	ection Date: 30th June 204			Time: 09			130-1030		
DSD	oted By: M.H. 公 sentative: <u>K.K. ()</u>	E&M Contractor  Representative:			S.M. Ho Y.H. Hory,	s kenneth Leany Frankie Chan			
	nmental Inspector: Tala	y Yemon							
Weath	per								
Conditio	on Sunny	Fine Over	cast	 Drizzle	R	ain	Storm	Hazy	
Temper	rature 23 °C	C Humi	dity	70 %	6				
Wind	<b>√</b> Calm	Light Bree	] ze :	Strong	l	Directior			
Ref. No. <sup>(1)</sup>	Brief Description	Site Location <sup>(2)</sup>	Yes	tivity Co	ompliai N/A	unk	Action Re Responsibl		
Air Qu	uality - Dust			<u> </u>					
1	Water spray	F, J, K, L, M, N, O, P, Q, R, S			V				
2	Cover debris				V				
3	Wet & cover stockpile				V				
4	Skip hoist	The state of the s			V				
5	Vehicle washing				V				
6	Clear of dusty materia				/				
7	Water spray on road				V_				
8	Cement bags				V				
9	Dusty material				1				
10	Cover belt conveyor				/				
Water (	Quality								
11	Storm drains	P. C. K.S.							
12	Sand/silt removal facilities	0,00,00		,					
13	Exposed soil surface								
14	Rainwater silt removal		V						
15	Open stockpiles			,					
16	Groundwater silt								

Ref.	Brief Description	Site	ļ	tivity (	Complia	nce	Action Required/
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3</sup>
17	Large object	F, J.K, L, M, 10, 0, P.Q., R,S			V		
18	Sewage discharged		V				
19	Fuel/chemical storage		J				
20	Storage area condition		1				
21	Clean-up actions	1	V				
Noise	Control						
22	Comply with ordinance	F, J, K, L, M, NO; P, Q, K, S					
23	Working equipment & sound-reducing measures				U		
24	Equipment condition		1				
25	Well-maintained plant				·~		
26	intermittent use of machines/plants				0		
27	Noise in one direction				1		
28	Silencers/mufflers				1		
29	Away from NSRs				ン		
30	Trial for equipment/sound-reducing measures				<b>V</b>		
Waste	Disposal	<u> </u>			<del> </del>		
31	Construction wastes	F,3,8,12,18,16,10, P, G, E, S	レ				
32	Licensed waste collector	6,5,5			.v		
33	Removal of construction wastes		V				
34	Waste storage areas		V				
35	Windblown litter/dust				V		
36	Waste disposal permits				V		
37	Licensed waste disposal facilities		0				
38	Careful design, planning & good site management				1		
39	Bentonite slurries				V		
10	Chemical wastes handling		1				
, ,	Chemical waste storage		V				
	Condition of chemical waste storage area						

Ref.	Brief Description	Site	Ac	tivity C	Complia	Action Required/	
No. <sup>(1)</sup>	of Mitigation	Location <sup>(2)</sup>	Yes	No	N/A	Unk	Responsible Party <sup>(3)</sup>
43	Disposal of chemical wastes	F, S, K, L, M, N, ,			V		
44	General refuse		1				
45	Chemical waste separation		V				
46	Strictly prohibited of refuse burning	D Carrier of D	0				
47	Environmental Permit and other documents on-site	The same of the sa	V	;			
48	Environmental Permit and license displayed	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	V				
49	Waste records	7	0				

49	Waste records	\ \ \ \ \ \	V					
	ary / Remarks <sup>(4)</sup>							
Installat Studge Studge Studen	tion reports Ares House Conditioning	of EAIM Extension Tente	eamp , At and	ment r Blow Deodov	were m t	eb louve For	sened No. 2, Tet	at
<b>(</b> )9	partamen	observation.			/No. 10	C- 1144		4\
Signatu	rac	<u></u>			(Note: Rei	rer to att	ached site la	yout)
<i>Signatu</i> DSD	Representative		E	&M Contr	actor Re	epreser	ntative	

Name:

M. HYTUEN

ame: A cuc x

Environmental Team Leader

Name:

House Lair

- Refer to Site Inspection Checklist Attachment for complete description (Summarized EM&A Manual) of referenced mitigation measure or requirement.
- <sup>(2)</sup> Indicate exact locations as indicated (by code) on the attached site layout.
- Note actions'plans and responsible party regarding any non-compliance in this column.
- 141 To be filled out by the environmental team.

### **Deficiency Investigations Reports**

(Not Applicable)

Complaint Reports

(Not Applicable)

### Summons and Prosecutions Records

(Not Applicable)

### **Permits**

- Environmental Permit (Same as in June 2006 Report)
- Notification from EPD regarding The Completion of Registration as a Chemical Waste Producer (Same as in June 2007 Report)
