Jardine Engineering Corporation Limited

Contract No. DE/2009/09 Construction of Tai Po Sewage Treatment Works - Stage V Phase II B

> **Quarterly Environmental** Monitoring and Audit Report (July to September 2012)

> > (Version 1.0)

Certified By

(Environmental Team Leader)

REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties.

CINOTECH CONSULTANTS LTD

Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388

Email: info@cinotech.com.hk

TABLE OF CONTENTS

		Page
E	XECUTIVE SUMMARY	1
	INTRODUCTION	
	ENVIRONMENTAL MONITORING AND AUDIT WORKS	
	ENVIRONMENTAL COMPLAINT AND PROSECUTION.	
	ENVIRONMENTAL LICENSING AND PERMITTING	
	FUTURE KEY ISSUES	
1.		
	BACKGROUND	
	PROJECT ORGANIZATIONS	
	TABLE 1.1 KEY PROJECT CONTACTS	
	CONSTRUCTION PROGRAMME AND SYNOPSIS OF WORK	
	SUMMARY OF EM&A REQUIREMENTS	
2.	-	
	MONITORING PARAMETERS AND MONITORING LOCATIONS	
	MONITORING METHODOLOGY AND CALIBRATION DETAILS	
	ENVIRONMENTAL QUALITY PERFORMANCE LIMITS (ACTION AND LIMIT LEVELS)	
	ENVIRONMENTAL MITIGATION MEASURES	6
3.	MONITORING RESULTS	7
	WEATHER CONDITIONS	7
	Air Quality	
	TABLE 3.1 MEASURED PARAMETERS AND RESULTS OF THE TSP LEVEL BASELINE CHECKING	7
	CONSTRUCTION NOISE	7
4.	AUDIT RESULTS	8
	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	8
	SITE AUDIT SUMMARY	
	TABLE 4.1 OBSERVATIONS AND RECOMMENDATIONS OF SITE AUDIT	
	STATUS OF ENVIRONMENTAL LICENSING AND PERMITTING	
	ADVICE ON WASTE MANAGEMENT STATUS	9
5.	,	40
P	ERFORMANCE LIMITS (ACTION AND LIMIT LEVELS)	
	SUMMARY OF EXCEEDANCES.	
	REVIEW OF THE REASONS FOR AND THE IMPLICATIONS OF NON-COMPLIANCE	10
6.	ENVIRONMENTAL COMPLAINTS AND PROSECUTIONS	11
7.	COMMENTS, CONCLUSIONS AND RECOMMENDATIONS	12
	EFFECTIVENESS OF MITIGATION MEASURES.	12
	CONCLUSION	12
	RECOMMENDATIONS	14

LIST OF TABLE

Table I	Summary Table for Events Recorded in the Reporting Quarter
Table 1.1	Key Project Contacts
Table 3.1	Measured Parameters and Results of the TSP Level Baseline Checking
Table 4.1	Observations and Recommendations of Site Audit

LIST OF FIGURES

riguit 1.1 Site Layout Fian	Figure 1.1	Site Layout Plan
-----------------------------	------------	------------------

Figure 1.2 Locations of Air Quality and Noise Monitoring Stations

LIST OF APPENDICES

Construction Programme
Monitoring Requirements
Action and Limit Levels
Graphical Presentation of 1-hour TSP Monitoring Results
Graphical Presentation of 24-hour TSP Monitoring Results
Graphical Presentation of Noise Monitoring Results
Updated Environmental Mitigation Implementation Schedule
Summary of Environmental Licensing and Permit Status
Waste Generation in the Reporting Quarter
Summary of Exceedance
Complaint Log

EXECUTIVE SUMMARY

Introduction

- 1. This is the 5th Quarterly Environmental Monitoring and Audit (EM&A) Summary Report prepared by Cinotech Consultants Limited (the Environmental Team, ET) for DSD Contract no. DE/2009/09 "Supply and Installation of Electrical and Mechanical Equipment for Tai Po Sewage Treatment Works Stage 5 Phase 2B". This summary report presents EM&A works performed in the period between July and September 2012.
- 2. The construction activities undertaken in the reporting quarter include:
 - Bolt torque and leakage test for penstocks at Flow Distribution Chamber No. 2;
 - Dismantling the existing temporary genset at Inlet Works G/F;
 - Fabrication of bio-gas holder on site;
 - Installation of bio-gas pipework in Pipe Gallery;
 - Installation of new centrifuge at SAS Thickening House:
 - Installation of new MCC4 and BS equipment at Chemical House;
 - Installation of new sludge dewatering system in Sludge Dewatering House Extension;
 - Installation of penstocks at Sludge Draw-off Chamber No. 4;
 - Installation of UPS at CBC and Chemical House;
 - Migration of Bridge Mount Mixers from Temporary Panel at RAS P/S to New MCC4 at Chemical House;
 - Modification of SCADA system at SAS thickening house;
 - Preparation of bolt torque test for penstocks at Flow Distribution Chamber No. 2;
 - Screeding for the bottoms of FC No. 11B and FC No. 12B;
 - Setup and energisation of power distribution board for load diversion before replacement of existing LV switchboards at Inlet Works G/F & 1/F;
 - Site modification of existing switchboard compartment for Filtrate Pumping Station; and
 - Site survey at the screw pump chamber of inlet works.

Environmental Monitoring and Audit Works

- 3. Environmental monitoring and audit works for the Project was performed regularly as stipulated in the EM&A Manual and the results were checked and reviewed. The implementation of the environmental mitigation measures, Event Action Plans and environmental complaint handling procedures were also checked.
- 4. Summary of the events and action taken in the reporting quarter is tabulated in **Table I**.

Table I Summary Table for Events Recorded in the Reporting Quarter

Donomoton	No. of Exceedance			Antion Talen
Parameter	Action Level	Limit Level	due to this Project	Action Taken
1-hour TSP	0	0	0	N/A
24-hour TSP	0	0	0	N/A
Noise	0	0	0	N/A

Construction Noise

5. All construction noise monitoring was conducted as scheduled in the reporting quarter. No Action Level (public complaint) / Limit Level exceedance was recorded in the reporting quarter.

Air Quality

6. The air quality monitoring was conducted as scheduled in this reporting period. No Action/Limit Level exceedance was recorded in the reporting period.

Environmental Complaint and Prosecution

7. No environmental complaint, prosecution or notification of summons was received in this reporting quarter.

Environmental Licensing and Permitting

8. Environmental related licenses/permits granted to the Project include the Environmental Permit (EP) for the Project.

Future Key Issues

- 9. The anticipated environmental impacts will be mainly on ponding water and surface runoff after rain as well as the noise nuisance and dust emission from the major construction activities will be undertaken in the coming quarter, including:
 - Bolt torque and leakage test for penstocks at Sludge Draw-off Chamber No. 4;
 - Installation of submersible sludge pump at Sludge Draw-off Chamber No. 4;
 - Installation of pinch valve, flowmeter and associated pipework at Flowmeter Chamber No. 1B:
 - Testing and commissioning of Final Clarifier No. 11B & 12B (including process instruments);
 - Fabrication of bio-gas holder on site;
 - installation of new sludge dewatering system and sludge feed pump in Sludge Dewatering House Extension;
 - Installation of new centrifuge and associated pipework & electrical work at SAS Thickening House;
 - T&C of new MCC4 (functions related to FC No. 11B & 12B) and installed BS equipment at Chemical House;
 - Installation of outdoor AC units at Chemical House roof;
 - Installation of lightning protection pole at Chemical House;
 - Migration of Submersible Mixers from Existing MCC3 at RAS PS to New MCC4 at Chemical House;
 - Setup & Energization of Power Distribution Board for the Replacement of Existing SWB at IW 1F & GF;
 - Load Diversion of Existing E&M Equipment from MCC1 to MCC2A Part 1 Cabling Works:
 - T&C of PLC H and SCADA (functions related to FC No. 11B& 12B;
 - Installation of optical fiber between PLC H and PLC E;
 - Modification of SCADA system at SAS thickening house; and
 - T&C of UPS at CBC and Chemical House.

1. INTRODUCTION

Background


- 1.1 Tai Po Sewage Treatment Works (TPSTW) is located within the Tai Po Industrial Estate. It currently comprises four Stages: I, II, IVA and IVB works. The TPSTW Stage V aims to upgrade the existing STW to provide additional sewage treatment capacity from the present design flow of 88,000 m³/day to 130,000 m³/day to meet the demands of both the existing and future developments, and to meet the revised discharge license requirements.
- 1.2 The TPSTW Stage V, Phase I and Phase II are Designated Projects under the Environmental Impact Assessment Ordinance (Cap. 449) with the same EIAO Register No. AEIAR 081/2004. A study of environmental impact assessment (EIA) was undertaken to evaluate various environmental impacts associated with the works within these two Designed Projects. An EIA Report as well as an Environmental Monitoring and Audit (EM&A) Manual were approved by the Environmental Protection Department (EPD) on 28 October 2004.
- 1.3 The Stage V works will be implemented in 2 phases. The design capacities of Phase I and Phase II works are 100,000 m³/day and 130,000 m³/day respectively. An Environmental Permit (EP) No. EP-265/2007 was issued on 22 March 2007 for the TPSTW Stage V Phase II to the Drainage Services Department (DSD) as the Permit Holder. The project "Tai Po Sewage Treatment Works Stage V Phase IIB" formed part of the Phase II works, includes additional secondary treatment process units (1 primary clarifier; 3 bioreactors and 2 final clarifiers) in TPSTW for its future extended plant design capacity of 120,000 m³/day. A master construction programme of the Project is provided in **Appendix M**. A site layout plan is provided in **Figure 1.1**. The construction activities of the Project commenced on 16 May 2011.
- 1.4 Cinotech Consultants Ltd. was commissioned by the Contractor as the Environmental Team (ET) to undertake the EM&A works for the Project. Dr. Priscilla CHOY of Cinotech Consultants Ltd. was appointed as the ET Leader as per the Condition 2.1 of the EP. Ove Arup and Partners Hong Kong Limited. was appointed as the IEC under Condition 2.2 of the EP. This is the 5th quarterly EM&A summary report summarizing the EM&A works for the Project between July and September 2012.

Project Organizations

- 1.5 Different parties with different levels of involvement in the project organization include:
 - Project Proponent / Engineer's Representative (ER) Drainage Services Department
 - Environmental Team (ET) Cinotech Consultants Ltd.
 - Independent Environmental Checker (IEC) Ove Arup and Partners Hong Kong Limited
 - Contractor Jardine Engineering Corporation Ltd.
- 1.6 The responsibilities of respective parties are detailed in Section 1.10 of the Final EM&A Manual of the Project.

Quarterly EM&A Summary Report – July to September 2012

1.7 The Project Organization during Construction Phase



1.8 The key contacts of the Project are shown in **Table 1.1**.

Table 1.1 Key Project Contacts

Party	Role	Name	Position	Phone No.	Fax No.	
DSD	E&M Branch	Mr. TONG Sau Kit	Senior Engineer	2594 7304	2827 8532	
טאט	EXIVI DIANCII	Mr. TSE Ho	Engineer	2660 7638	2821 8332	
		Dr. Priscilla CHOY	ET Leader	2151 2089		
Cinotech	Environmental Team	Mr. Ken CHENG	Project Coordinator and Audit Team Leader	2151 2077	3107 1388	
		Mr. Henry LEUNG	Monitoring Team Leader	2151 2087		
Arma	Independent Environmental	Mr. Coleman NG	Independent Environmental Checker	2268 3097	2865 6493	
Arup	Checker	Mr. Lawrence KAN	Assistant to Independent Environmental Checker	2268 3212	2803 0493	
	E & M	Mr. Alex Law	Project Manager	9312 8659		
JEC	E&M Contractor	Mr. Dexter Chan	Site Agent	6391 2499	2887 9090	
	Contractor	Mr. Brendan Chan	Environmental Officer	6393 2904		

Construction Programme and Synopsis of Work

- 1.9 The construction programme is presented in **Appendix A**. The site activities undertaken during the reporting quarter included:
 - Bolt torque and leakage test for penstocks at Flow Distribution Chamber No. 2;
 - Dismantling the existing temporary genset at Inlet Works G/F;
 - Fabrication of bio-gas holder on site;
 - Installation of bio-gas pipework in Pipe Gallery;
 - Installation of new centrifuge at SAS Thickening House;
 - Installation of new MCC4 and BS equipment at Chemical House;
 - Installation of new sludge dewatering system in Sludge Dewatering House Extension;
 - Installation of penstocks at Sludge Draw-off Chamber No. 4;
 - Installation of UPS at CBC and Chemical House;
 - Migration of Bridge Mount Mixers from Temporary Panel at RAS P/S to New MCC4 at Chemical House;
 - Modification of SCADA system at SAS thickening house;
 - Preparation of bolt torque test for penstocks at Flow Distribution Chamber No. 2;
 - Screeding for the bottoms of FC No. 11B and FC No. 12B;
 - Setup and energisation of power distribution board for load diversion before replacement of

existing LV switchboards at Inlet Works G/F & 1/F;

- Site modification of existing switchboard compartment for Filtrate Pumping Station; and
- Site survey at the screw pump chamber of inlet works.

Summary of EM&A Requirements

- 1.10 The EM&A programme requires construction phase air quality, noise monitoring and landfill gas monitoring as well as environmental site audits. The EM&A requirements are described in the following sections, including:
 - All monitoring parameters;
 - Action and Limit levels for all environmental parameters;
 - Event / Action Plans;
 - Environmental mitigation measures, as recommended in the project EIA study final report; and
 - Environmental requirements in contract documents.
- 1.11 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 4 of this report.
- 1.12 This report presents the monitoring results, observations, locations, equipment, period, methodology and QA/QC procedures of the required monitoring parameters, namely air quality and noise as well as audit works for the Project in the reporting period.

2. ENVIRONMENTAL MONITORING AND AUDIT REQUIREMENTS

Monitoring Parameters and Monitoring Locations

- 2.1 The EM&A Manual designate locations for the ET to monitor environmental impacts in terms of noise and air quality due to the Project. The Project area and monitoring locations are depicted in **Figure 1.2**. **Appendix B** gives details of monitoring requirements.
- 2.2 In accordance with clause 8.8 of the EM&A Manual, the number and location of the monitoring stations and parameters can be referred to Monthly EM&A reports in order to cater for any changes in the surrounding environmental and the nature of works in progress. In the reporting months, there is no alteration made on changing the location of the monitoring stations.
- 2.3 In accordance with clause 2.30 of the EM&A Manual, baseline checking of ambient Total Suspended Particulates (TSP) levels shall be carried out every six months at each monitoring location, when no dusty works activities are in operation. This provides data for the determination of the appropriate Action levels with the Limit levels set against statutory or otherwise agreed limits. A TSP baseline checking was conducted in July 2012 in accordance to the requirement stipulated in the EM&A Manual. The results are detailed in Section 3 of this report. The current Action and Limit levels for 1-hour TSP and 24-hour TSP monitoring are still representative and valid after considered results obtained the baseline checking.

Monitoring Methodology and Calibration Details

2.4 Monitoring works/equipments were conducted/calibrated regularly in compliance with the EM&A Manual's requirements. Monitoring methodologies and calibration details can be referred to Monthly EM&A reports. Valid calibration certificates were attached in the appendices of the relevant Monthly EM&A reports.

Environmental Quality Performance Limits (Action and Limit Levels)

2.5 The environmental quality performance limits, i.e. Action and Limit Levels were derived from the baseline monitoring results. Should the measured environmental quality parameters exceed the Action/Limit Levels, the respective action plans would be implemented. The Action/Limit Levels for each environmental parameter are given in **Appendix C**.

Environmental Mitigation Measures

2.6 Relevant mitigation measures as recommended in the project EIA report have been stipulated in the EM&A Manual for the Contractor to implement. A summary of the Updated Environmental Mitigation Implementation Schedule (EMIS) is given in **Appendix H**.

3. MONITORING RESULTS

Weather Conditions

3.1 The weather during monitoring sessions was mainly sunny or cloudy. The weather conditions for each individual monitoring session were presented in corresponding of Monthly EM&A Reports.

Air Quality

- 3.2 Air quality monitoring was conducted as scheduled in the reporting period.
- 3.3 Graphical presentations of 1-hour TSP and 24-hour TSP monitoring results are shown in **Appendices D** and **E**, respectively.
- 3.4 All measured 1-hour and 24-hour TSP levels were below the Action/Limit Levels. No exceedance was recorded in the reporting quarter.
- 3.5 1-hour and 24-hour TSP baseline checking was conducted in July 2012 in accordance with clause 2.30 of the EM&A Manual. The baseline checking results for 1-hour TSP is within the range of baseline monitoring results presented in Baseline Monitoring Report. However, the baseline checking results for 24-hour TSP is below the range of baseline monitoring results presented in Baseline Monitoring Report. The monitoring dates and parameters are presented in **Table 3.1**.

Table 3.1 Measured Parameters and Results of the TSP Level Baseline Checking

Parameter	Monitoring Date	Monitoring Station	Average Baseline Checking Result (Range)	Average Baseline Monitoring Result (Range)
1-hour	26,27 and 28 July 2012	CAM1	68 (64-75)	100 (46-208)
TSP	(During Lunch Hour)	CAM2	85 (73-96)	132 (56-219)
131		CAM3	90 (87-94)	144 (77-240)
24 h	20 Il., 2012	CAM1	24	63 (39-116)
24-hour TSP	29 July 2012	CAM2	CAM2 29 72 (43-130)	72 (43-130)
131	(Sunday)	CAM3	40	95 (60-159)

3.6 The rather low TSP level obtained in the baseline checking might consider being a consequence of heavy rain episodes during the period when the 1-hour TSP and 24-hour TSP baseline checking carried out. The baseline checking result is primarily affected by rainy weather but not significant changes in the ambient conditions in the vicinity of the Contract. Therefore, the current Action and Limit levels for 1-hour TSP and 24-hour TSP monitoring are still representative and valid.

Construction Noise

- 3.7 All construction noise monitoring was conducted as scheduled in the reporting period.
- 3.8 Graphical representations of the monitoring results are shown in **Appendix F**. No Action Level (public complaint) / Limit Level exceedance was recorded in the reporting period.

Quarterly EM&A Summary Report – July to September 2012

4. AUDIT RESULTS

Implementation Status of Environmental Mitigation Measures

4.1 The implementation status of environmental mitigation measures (EMIS) is given in **Appendix H**.

Site Audit Summary

4.2 During site inspections in the reporting period, no non-conformance was identified. The observations and recommendations made in each site audit session in the reporting period are summarized in **Table 4.1**.

Table 4.1 Observations and Recommendations of Site Audit

Parameters	Date	Observations and Recommendations	Follow-up
	5 Jul 2012	Reminder: - Clear the rain water pond on the haul road near site office.	The situation was observed rectified during the audit session on 13 Jul 2012.
	13 Jul 2012	Reminder: - Stagnant water at FC12B should be pumped out.	The situation was observed rectified during the audit session on 19 Jul 2012.
	27 Jul 2012	Reminder: - Stagnant water near site office should be cleared after rainstorm.	The situation was rectified by the Contractor on 28 Jul 2012.
	9 Aug 2012	Reminder: The stagnant water at FC11B should be removed and pumped out into appropriate watercourse.	The situation was observed rectified by the Contractor during the audit session on 21 Aug 2012.
Water Quality	17 Aug 2012	Reminder: The stagnant water at SAS thickening house should be removed.	As claimed by the Contractor, the stagnant water at SAS thickening house comes from the existing operating centrifugal system but not arising from the construction work of the Contractor.
	17 Aug 2012	Reminder: The stagnant water at FC11B & FC12B should be removed and pumped out into appropriate watercourse after rainstorm.	The situation was observed rectified by the Contractor during the audit session on 21 Aug 2012.
	21 Aug 2012	Reminder: The sand and silt on the haul road outside Biogas holder should be removed.	The situation was rectified by the Contractor after the audit session on 21 Aug 2012.
	28 Aug 2012	The stagnant water at FC12B should be removed and pumped out into appropriate watercourse after rainstorm.	The observation was observed improved/rectified by the Contractor during the audit session on 6 Sep 2012.
	6 Sep 2012	Reminder: The stagnant water at FC12B should be removed and pumped out into appropriate watercourse after rainstorm.	The observation was improved/rectified by the Contractor on 11 Sep 2012.
	14 Sep 2012	Reminder: The stagnant water at and FC11B and FC12B should be removed and pumped out into appropriate watercourse.	The observation was observed improved/rectified by the Contractor during the audit session on 20 Sep 2012.

Parameters	Date	Observations and Recommendations	Follow-up	
	20 Sep 2012	Reminder: The stagnant water at and FC11B and FC12B should be pumped out.	The observation was observed improved/rectified by the Contractor during the audit session on 26 Sep 2012.	
	26 Sep 2012	Reminder: Soil water accumulated at FC11B should be pumped out.	Follow up action is needed to be reviewed in the next reporting period.	
Air Quality				
Noise				
	5 Jul 2012	Reminder: - Cover the exposed C&D waste on the rubbish bin near site office with impervious sheet.	The observation was observed rectified during the audit session on 13 Jul 2012.	
Waste / Chemical	27 Jul 2012	Reminder: The C&D waste should be removed in chemical house.	The observation was observed rectified by the Contractor during the audit session on 2 Aug 2012.	
Management		Follow up action is needed to be reviewed in the next reporting period.		
	26 Sep 2012	Reminder: Debris and litter near FC11B should be removed.	Follow up action is needed to be reviewed in the next reporting period.	

Status of Environmental Licensing and Permitting

4.3 Environmental licenses and permits including the Environmental Permit (EP), the Construction Noise Permit and Waste Disposal (Chemical Waste) License were in place and valid during the reporting quarter. A summary of environmental licensing and permit status is given in **Appendix I**.

Advice on Waste Management Status

4.4 No inert C&D waste was disposed in the reporting period. 3.6 tonne of general refuse was disposed in the reporting period. No chemical waste was generated in the reporting period. The amount of wastes generated by the activities of the Project in the reporting period fulfills the requirement of estimated volume of excavated material in EIA Report. The amount of wastes generated by the activities of the Project in the reporting period was attached in the appendices of the Monthly Reports for July to September 2012. Waste flow table please refer to **Appendix J**.

5. NON-COMPLIANCE (EXCEEDANCES) OF THE ENVIRONMENTAL QUALITY PERFORMANCE LIMITS (ACTION AND LIMIT LEVELS)

Summary of Exceedances

- 5.1 Environmental monitoring works were performed in the reporting period and all monitoring results were checked and reviewed. A summary of exceedance is attached in **Appendix K**.
- 5.2 All measured 1-hour and 24-hour TSP levels were below the Action/Limit Levels. No exceedance was recorded in the reporting period.
- 5.3 No Action/Limit Level exceedance for the construction noise was recorded in the reporting period.

Review of the Reasons for and the Implications of Non-compliance

5.4 There was no non-compliance from the site audits in the reporting quarter. The observations and recommendations made in each audit session were attached in the Monthly Reports.

6. ENVIRONMENTAL COMPLAINTS AND PROSECUTIONS

No environmental related complaint, prosecution or notification of summons was received in the reporting quarter.

7. COMMENTS, CONCLUSIONS AND RECOMMENDATIONS

7.1 Environmental monitoring and audit works were performed in the reporting quarter. The EM&A program was strictly following the requirement of methodology in EM&A manual. The monitoring work was considered as effective. In addition, site inspections were conducted on a weekly basis. The results were reviewed and checked.

Effectiveness of Mitigation Measures

7.2 The mitigation measures recommended in the EIA report and required by the EP are considered effective in minimizing environmental impacts. The Contractor has implemented the recommended mitigation measures except those mitigation measures not applicable at this stage.

Conclusion

- 7.3 All measured 1-hour and 24-hour TSP levels were below the Action/Limit Levels. No exceedance was recorded in the reporting quarter.
- 7.4 All measured noise levels were below the Action/Limit Levels. No exceedance was recorded in the reporting quarter.
- 7.5 There was no environmental complaint, prosecution or notification of summons received.
- 7.6 The anticipated environmental impacts will be mainly on ponding water after rain as well as the noise nuisance and dust emission from the major construction activities will be undertaken in the coming quarter, including:
 - Bolt torque and leakage test for penstocks at Sludge Draw-off Chamber No. 4;
 - Installation of submersible sludge pump at Sludge Draw-off Chamber No. 4;
 - Installation of pinch valve, flowmeter and associated pipework at Flowmeter Chamber No. 1B:
 - Testing and commissioning of Final Clarifier No. 11B & 12B (including process instruments):
 - Fabrication of bio-gas holder on site;
 - installation of new sludge dewatering system and sludge feed pump in Sludge Dewatering House Extension;
 - Installation of new centrifuge and associated pipework & electrical work at SAS Thickening House;
 - T&C of new MCC4 (functions related to FC No. 11B & 12B) and installed BS equipment at Chemical House;
 - Installation of outdoor AC units at Chemical House roof;
 - Installation of lightning protection pole at Chemical House;
 - Migration of Submersible Mixers from Existing MCC3 at RAS PS to New MCC4 at Chemical House;
 - Setup & Energization of Power Distribution Board for the Replacement of Existing SWB at IW 1F & GF;
 - Load Diversion of Existing E&M Equipment from MCC1 to MCC2A Part 1 Cabling Works:
 - T&C of PLC H and SCADA (functions related to FC No. 11B& 12B;
 - Installation of optical fiber between PLC H and PLC E;

- Modification of SCADA system at SAS thickening house; and
- T&C of UPS at CBC and Chemical House.

Recommendations

7.7 According to the environmental audit sessions performed in the reporting period, the following recommendations were made:

Water Impact

• Avoid accumulation of stagnant water on site after rainstorm.


Dust Impact


- Excavated dusty materials or stockpile of dusty materials should be covered by impervious sheeting, or sprayed with water so as to maintain entire surface wet, if necessary.
- Remove fugitive dusty material on the haul road periodically.
- Spray with water on dry dust haul road.

Waste / Chemical Management


- Avoid and check for any accumulation of waste materials on site and dispose waste materials at designated areas.
- Provide bunded containers for the storage of chemical wastes at the waste storage area.

FIGURES

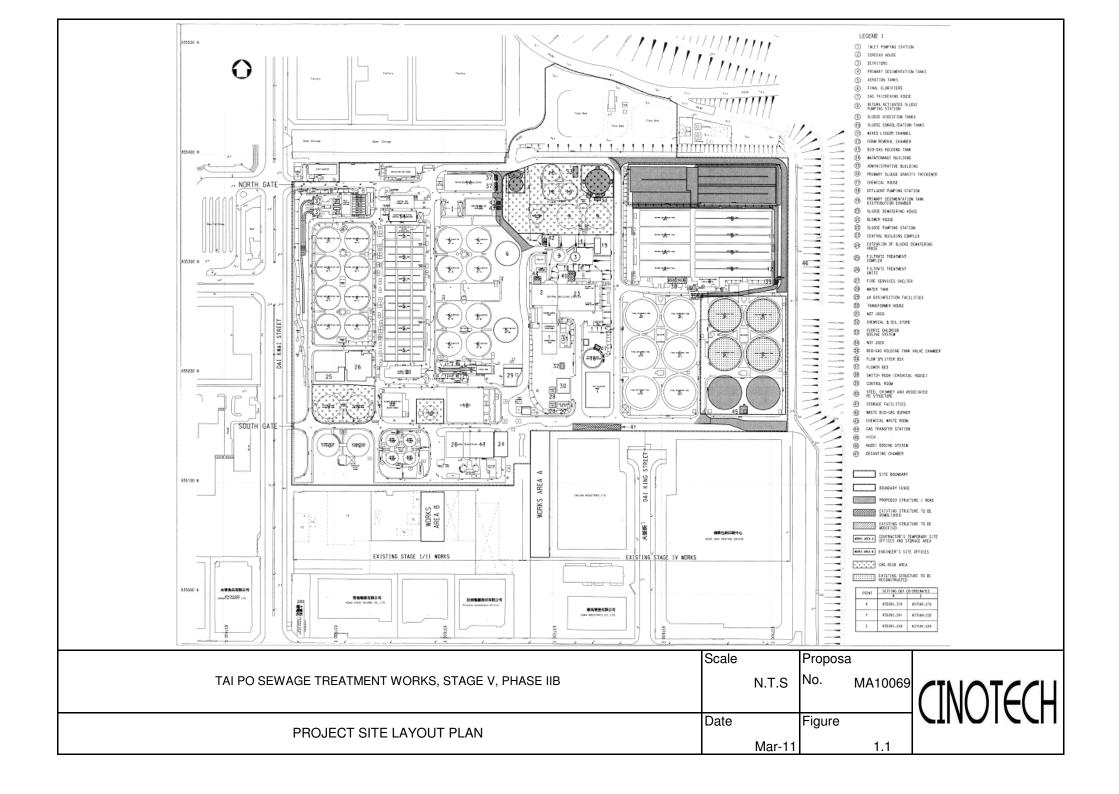

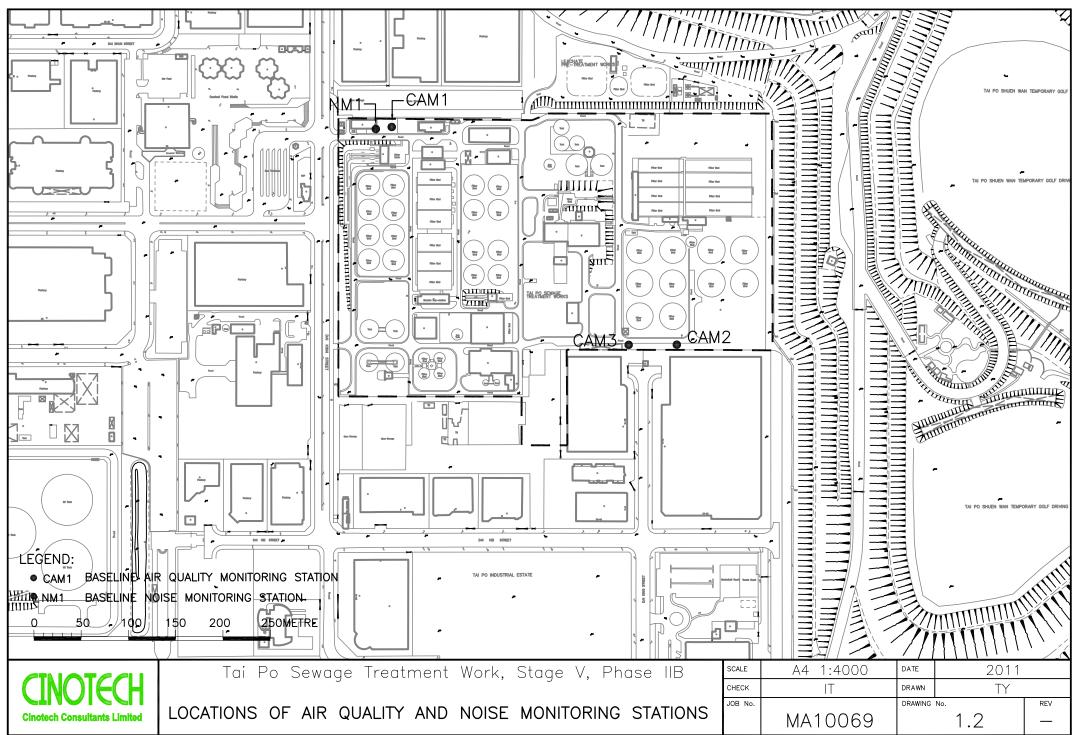

APPENDIX A CONSTRUCTION PROGRAMME

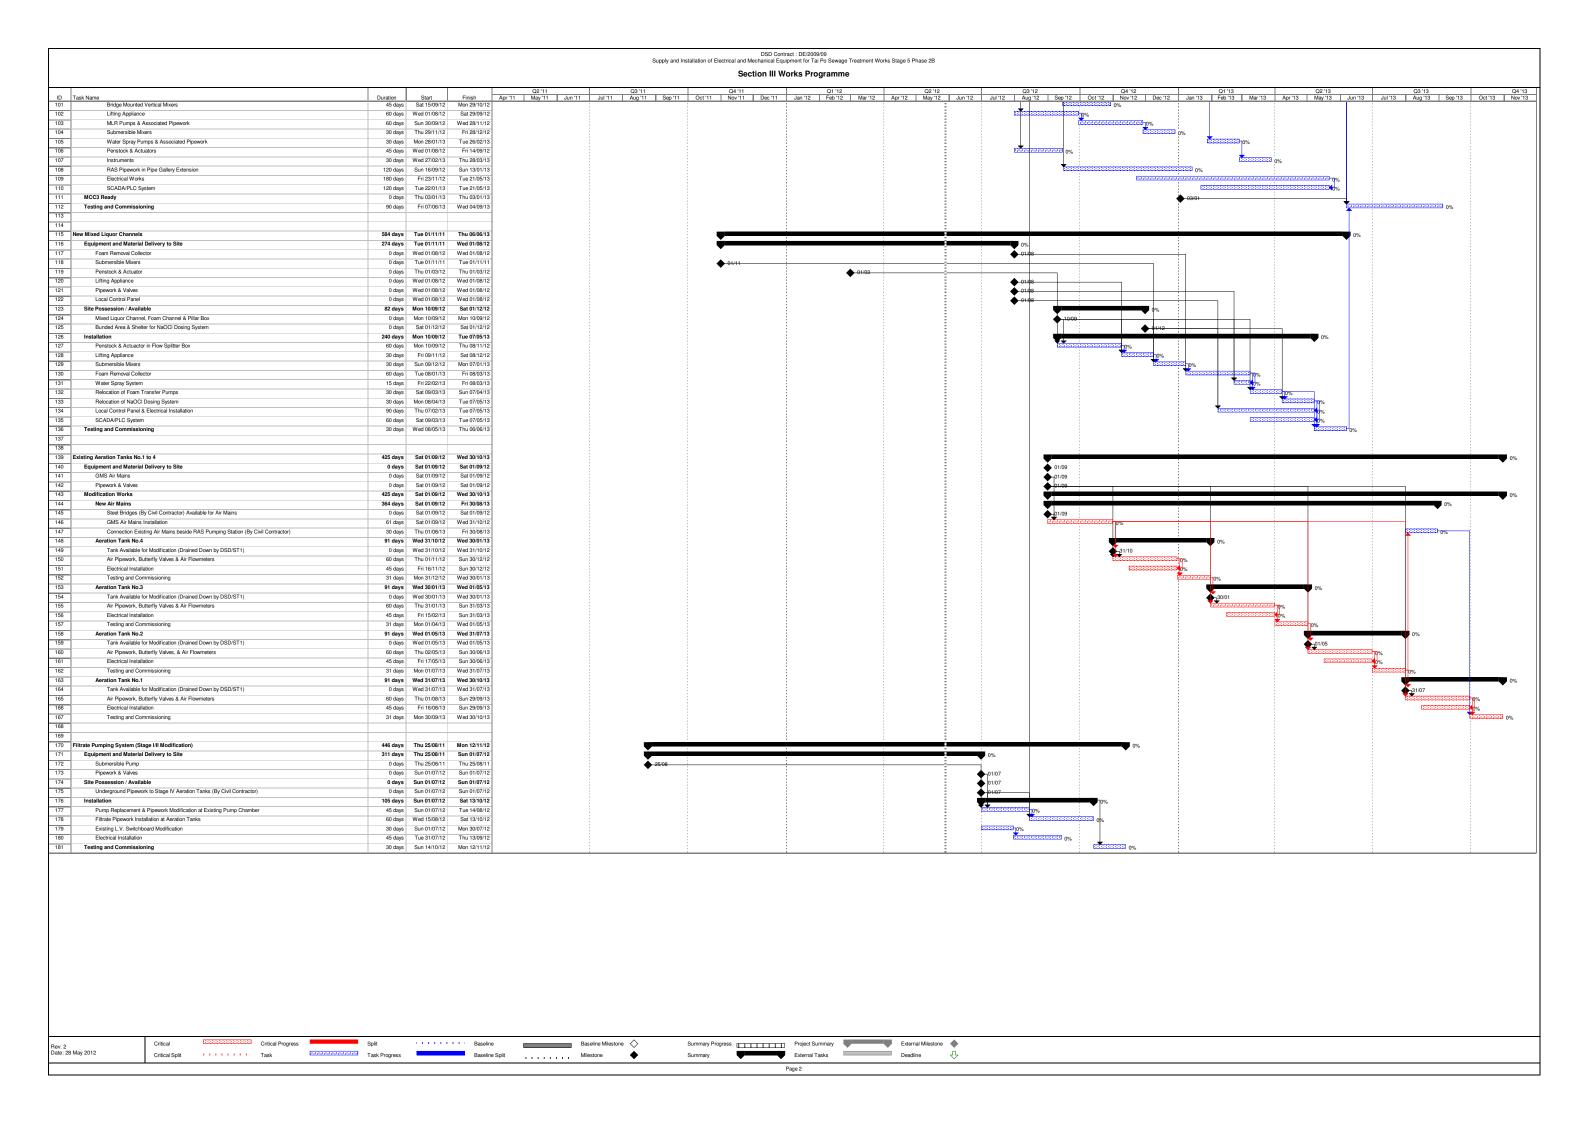

DSD Contract : DE/2009/09
Supply and Installation of Electrical and Mechanical Equipment for Tai Po Sewage Treatment Works Stage 5 Phase 2B Section V Works Programme Duration Start Finish 01'11 02'11 03'11 04'11 05'11 06'11 09'11 01'11 01'12 02'12 03'12 04'12 05'12 06'12 05'12 06'12 05'12 06'12 05'12 06'12 05'12 06'12 05'12 06'12 05'12 06'12 05 | Task Name | 201 | SAS Thickening System | 202 | Equipment & Material Delivery to Site 270 days Fri 01/06/12 Mon 25/02/13 34 days Fri 01/06/12 Thu 05/07/12 0 days Thu 05/07/12 Thu 05/07/12 0 days Fri 01/06/12 Fri 01/06/12 Centrifuge SAS Feed Pump 0 days Fri 01/06/12 Fri 01/06/12 0 days Fri 01/06/12 Fri 01/06/12 Polyelectrolyte Feed Pump Thickened Sludge Storage Tank 0 days Fri 01/06/12 Fri 01/06/12 0 days Fri 01/06/12 Fri 01/06/12 Pipework & Valves Vibration Monitoring System PLC System M Panel 0 days Fri 01/06/12 Fri 01/06/12 Site Possession / Available
Civil Works Provision (By Civil Contractor) 0 days Fri 01/06/12 Fri 01/06/12 0 days Fri 01/06/12 Fri 01/06/12 180 days Fri 01/06/12 Installation

Centrifuge, Vibration Monitoring System & Associated Accessories 30 days Thu 05/07/12 Fri 03/08/12 SAS Feed Pump & Associated Pipework

Polyelectrolyte Feed Pump & Associated Pipework 16 days Mon 03/09/12 Tue 18/09/12 Thickened Sludge Storage Tank & Associated Acces 30 days Sat 04/08/12 Sun 02/09/12 16 days Mon 03/09/12 Tue 18/09/12 90 days Fri 01/06/12 Wed 29/08/12 Centrate Pipework Existing L.V. Switchboard Modification 90 days Thu 30/08/12 Tue 27/11/12 60 days Sat 29/09/12 Tue 27/11/12 Electrical Installation SCADA/PLC System Testing & Commissioning 90 days Wed 28/11/12 Mon 25/02/13 446 days Thu 08/12/11 Mon 25/02/13 223 Sludge Dewatering System Equipment & Material Delivery to Site Membrane Filter Press 115 days Thu 08/12/11 Sun 01/04/12 0 days Mon 20/02/12 Mon 20/02/12 20/02 Sludge Feed Pump 0 days Thu 08/12/11 Thu 08/12/11 0 days Sun 01/04/12 Sun 01/04/12 Polyelectrolyte Dosing Pump Floctronic Sensor c/w Inline Mixer Pipework & Valves 0 days Fri 20/01/12 Fri 20/01/12 0 days Sun 01/04/12 Sun 01/04/12 PLC System K Panel 0 days Sun 01/04/12 Sun 01/04/12 Site Possession / Available
Civil Works Provision (By Civil Contractor) 0 days Sun 01/04/12 Sun 01/04/12 0 days Sun 01/04/12 Sun 01/04/12 275 days Mon 27/02/12 Tue 27/11/12 Installation

Membrane Filter Press 79 days Mon 27/02/12 Tue 15/05/12 30 days Wed 16/05/12 Thu 14/06/12 Sludge Feed Pump & Associ Polyelectrolyte Dosing Pump & Associated Pipework 30 days Fri 15/06/12 Sat 14/07/12 Filtrate Pipework

Existing L.V. Switchboard Modification & Electrical Installation 15 days Sun 15/07/12 Sun 29/07/12 90 days Fri 01/06/12 Wed 29/08/12 90 days Thu 30/08/12 Tue 27/11/12 60 days Sat 29/09/12 Tue 27/11/12 90 days Wed 28/11/12 Mon 25/02/13 SCADA/PLC System Testing and Commissioning 90 days Sat 01/09/12 Thu 29/11/12 244 Hybrid Street Light Installation, Testing & Commissioning
245 Automatic Weather Station Installation, Testing & Commissioning 90 days Sat 01/09/12 Thu 29/11/12 90 days Sat 01/09/12 Thu 29/11/12

APPENDIX B MONITORING REQUIREMENTS

APPENDIX B – MONITORING REQUIREMENTS

Type of Monitoring	Parameter	Frequency	Duration	Location of Measurement
Noise ⁽¹⁾	$L_{eq}(30 \text{ min.}) \label{eq:eq} \eqno(0700\text{-}1900 \text{ hrs. on normal weekdays})$	Once per week	30 mins	NM1 (Outside the corridor of 1/F of Government Staff Quarter)
	1-hour TSP	3 times every six days	1 hour	CAM1 (on flat roof of Government Staff Quarters)
Air	24-hour TSP	Once every six days	24 hours	 CAM2 (on ground within TPSTW and just next to the Printing Centre of Hung Hing Printing Centre) CAM3 (on ground within TPSTW and just next to Talcon Industrial Ltd.)

⁽¹⁾ If construction works are extended to include works during the hours of 1900 – 0700, additional weekly impact monitoring shall be carried out during evening and night-time works.

APPENDIX C ACTION AND LIMIT LEVELS

APPENDIX C – Action and Limit Levels

1-Hour TSP

Location	Action Level, μg/m ³	Limit Level, μg/m³
CAM1	315	
CAM2	336	500
CAM3	344	

24-Hour TSP

Location	Action Level, μg/m ³	Limit Level, μg/m ³
CAM1	171	
CAM2	177	260
CAM3	192	


Construction Noise

Time Period	Action Level	Limit Level
0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A)
0700-2300 hrs on holidays; and 1900- 2300 hrs on all other days		70* dB(A)
2300-0700 hrs of next day		55* dB(A)


Notes:

^{*} The Area Sensitivity Rating for Station NM1 is taken as C, due to the nearby industrial area, according to Table 1 of EPD's Technical Memorandum on Noise from Construction Work other than Percussive Piling.

APPENDIX D GRAPHICAL PRESENTATION OF 1-HOUR TSP MONITORING RESULTS

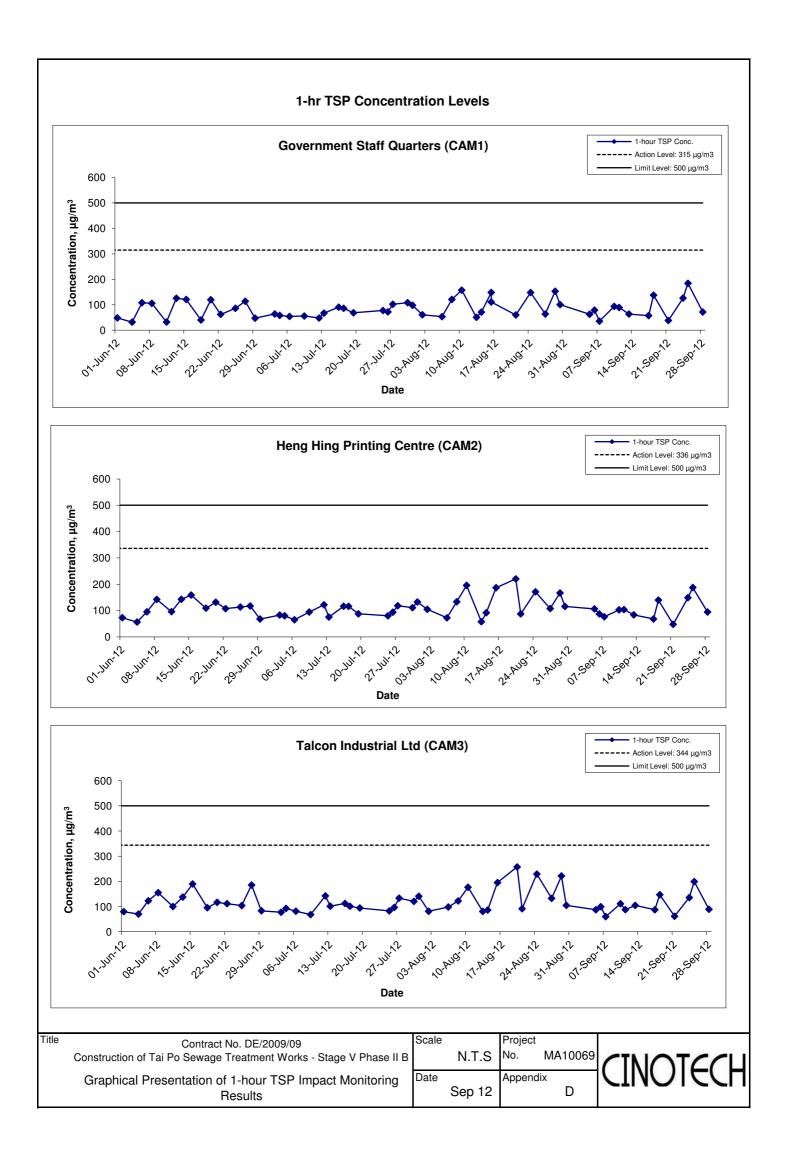


APPENDIX E GRAPHICAL PRESENTATION OF 24-HOUR TSP MONITORING RESULTS

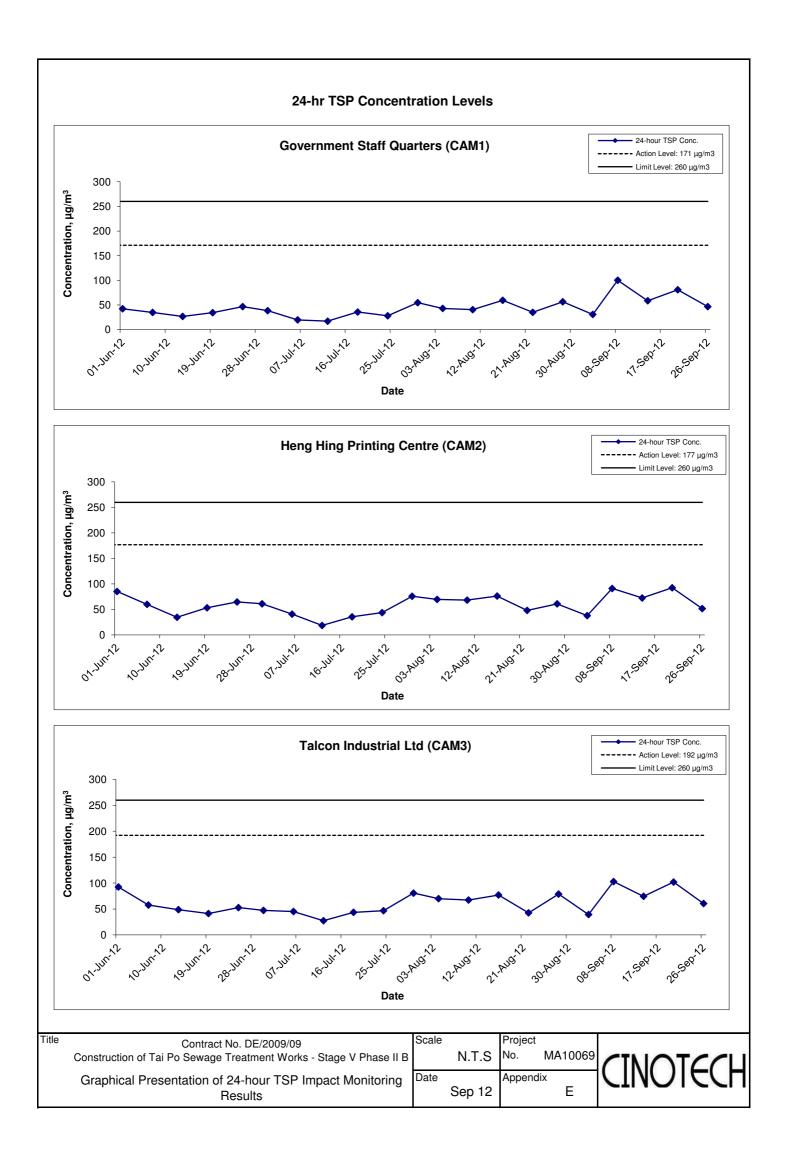

APPENDIX F GRAPHICAL PRESENTATION OF NOISE MONITORING RESULTS

Noise Levels

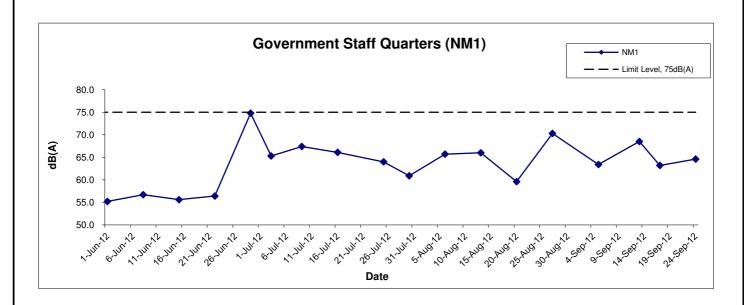

Title Contract No. DE/2009/09
Construction of Tai Po Sewage Treatment Works - Stage V Phase II B

Graphical Presentation of Construction Noise Monitoring Results

Scale		Project
		No.
	N.T.S	MA10069
Date		Appendix
	Sep 12	F



APPENDIX G UPDATED ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

APPENDIX G – Updated Environmental Mitigation Implementation Schedule (During Construction Phase)

Type of Impact	Recommended Mitigation Measures	Status				
Air Quality	Dust mitigation measures stipulated in <i>the Air Pollution Control (Construction Dust) Regulation</i> shall be incorporated to control dust emission. Notice shall be given to authority prior to commencing of work					
Noise	Use of quiet PME	N/A				
	 Good Site Practice Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program; Silencers or mufflers on construction equipment should be utilized and should be properly maintained during the construction program; Mobile plant, if any, should be sited as far from NSRs as possible; Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 	V				
Water Quality	The practices outlined in ProPECC PN 1/94 Construction Site Drainage should be adopted to minimize the potential water quality impacts from construction site runoff and various construction activities. The recommendation to install perimeter drains to collect site runoff and to properly treat the runoff by settlement tank/treatment system shall apply to all sites including those for mainlaying works. Minimum distances of 100 m should be maintained between the discharge points of construction site runoff and the existing WSD saltwater intake at Tai Po.					
	A discharge licence needs to be applied from EPD for discharging effluent from the construction site. The discharge quality is required to meet the requirements specified in the discharge licence. All the runoff and wastewater generated from the works areas should be treated so that it satisfies with all the standards listed in the TM. Reuse and recycling of the treated effluent can minimize water consumption and reduce the effluent discharge volume. The beneficial uses of the treated effluent may include dust suppression, wheel washing and general cleaning. Monitoring of the discharge quality of treated effluent should be part of the Environmental Monitoring and Audit (EM&A) programme. Detailed effluent sampling programme for water quality control during construction phase should be submitted to EPD, AFCD and WSD for approval prior to commencement of the construction works.	V				
	The construction programme should be properly planned to minimize soil excavation, if any, in rainy seasons. This prevents soil erosion from exposed soil surfaces. Any exposed soil surfaces should also be properly protected to minimize dust emission. In areas where a large amount of exposed soils exist, earth bunds or sand bags should be provided. Exposed stockpiles should be covered with tarpaulin or impervious sheets at all time. The stockpiles of materials should be placed in the locations away from any stream courses so as to avoid releasing materials into the water bodies. Final surfaces of earthworks should be compacted and protected by permanent work. It is suggested that haul roads should be paved with concrete and the temporary access roads are protected using crushed stone or gravel, wherever practicable. Wheel washing facilities should be provided at all site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles.	√				
	Good site practices should be adopted to clean the rubbish and litter on the construction sites so as to prevent the rubbish and litter from dropping into the nearby environment. It is recommended to clean the construction sites on a regular basis.	V				

Type of Impact	Recommended Mitigation Measures	Status
	It is recommended to provide sufficient chemical toilets in the works areas. The toilet facilities should not be less than 30 m from any watercourse. A licensed waste collector should be deployed to clean the chemical toilets on a regular basis. The construction workers can also make use of the existing toilet facilities within the TPSTW as necessary.	1
	Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the project. Implementation of environmental audit on the construction site can provide an effective control of any malpractices and can achieve continual improvement of environmental performance on site.	V
	It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	V
	Any service shop and minor maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken with the areas appropriately equipped to control these discharges.	V
	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows: • Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport • Chemical waste containers should be suitably labelled to notify and warn the personnel who are handling the wastes to avoid accidents. • Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.	V
	Marine water quality monitoring should be carried out under emergency condition or during maintenance of the THEES tunnel to verify the findings of the water quality modelling. It is recommended that the maintenance of the THEES tunnel, if unavoidable, should be conducted during winter season or low flow periods and to avoid the "blooming" season of algae (normally from April to June) if practicable. Details of the monitoring requirements are specified in the EM&A Manual.	N/A

Type of Impact	Recommended Mitigation Measures	Status					
Waste	Good site practices during the construction activities include:	1					
Management	Nomination of approved personnel, such as a site manager, to be responsible for good site						
J	practices, arrangements for collection and effective disposal to an appropriate facility, of all						
	wastes generated at the site.						
	Training of site personnel in proper waste management and chemical waste handling procedures.						
	Provision of sufficient waste disposal points and regular collection for disposal.						
	Appropriate measures to minimise windblown litter and dust during transportation of waste by						
	either covering trucks or by transporting wastes in enclosed containers.						
	Separation of chemical wastes for special handling and appropriate treatment at the Chemical						
	Waste Treatment Facility.						
	Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.						
	A Waste Management Plan shall be prepared and this WMP shall be submitted to the Engineer						
	for approval. One may make reference to ETWB TCW No. 15/2003 for details.						
	• In order to monitor the disposal of C&D materials at landfills and public filling areas, and to						
	control fly tipping, a trip-ticket system shall be included as one of the contractual requirements						
	and implemented by an Environmental Team undertaking the Environmental Monitoring and						
	Audit work. One may make reference to WBTC No. 21/2002 for details.						
	A recording system for the amount of wastes generated, recycled and disposed (including the						
	disposal sites) shall be proposed.						
	Waste reduction is best achieved at the planning and design stage, as well as by ensuring the						
	implementation of good site practices. Recommendations to achieve waste reduction include:						
	Segregation and storage of different types of waste in different containers, skips or stockpiles to						
	enhance reuse or recycling of materials and their proper disposal.						
	• To encourage collection of aluminum cans by individual collectors, separate labelled bins shall be						
	provided to segregate this waste from other general refuse generated by the work force.						
	,						
	ordering						
	General Refuse	V					
	General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A						
	reputable waste collector shall be employed by the contractor to remove general refuse from the site,						
	separately from C&D material. An enclosed and covered area is preferred to reduce the occurrence						
	of 'wind blown' light material.						
enhance reuse or recycling of materials and their proper disposal. To encourage collection of aluminum cans by individual collectors, separate labelled bins sh provided to segregate this waste from other general refuse generated by the work force. Any unused chemicals or those with remaining functional capacity shall be recycled. Maximize the use of reusable steel formwork to reduce the amount of C&D material. Prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimize the quantity of waste to be disposed of to landfill. Proper storage and site practices to minimize the potential for damage or contamination of construction materials. Plan and stock construction materials carefully to minimize amount of waste generated and a unnecessary generation of waste. Minimize over ordering of concrete, mortars and cement grout by doing careful check before ordering General Refuse General refuse shall be stored in enclosed bins or compaction units separate from C&D material reputable waste collector shall be employed by the contractor to remove general refuse from the separately from C&D material. An enclosed and covered area is preferred to reduce the occurre of 'wind blown' light material. Construction & Demolition (C&D) Material C&D material generated from the site formation and demolition works shall be sorted on-site in inert C&D material (i.e. public fill) and C&D waste. In order to minimise the impact resulting full collection and transportation of C&D material for off-site disposal, the excavated material							
	C&D material generated from the site formation and demolition works shall be sorted on-site into						
	inert C&D material (i.e. public fill) and C&D waste. In order to minimise the impact resulting from						
	collection and transportation of C&D material for off-site disposal, the excavated material						
	comprising fill material shall be reused on-site as backfilling material as far as practicable. C&D						
	waste, such as wood, plastic, steel and other metals shall be reused or recycled and, as a last resort,						
	disposed of to landfill. A suitable area shall be designated within the site for temporary stockpiling of						
	C&D material and to facilitate the sorting process.						

Quarterly EM&A Report

Type of Impact	Recommended Mitigation Measures	Status
	Bentonite Slurry	N/A
	Bentonite slurries used in construction works should be reconditioned and reused wherever	
	practicable. Residual used bentonite slurry should be disposed of from the site as soon as possible.	
	The Contractor should explore alternative disposal outlets for the residual used bentonite slurry and	
	disposal at landfill should be the last resort.	

Note: √ –

 $\sqrt{}$ – Compliance of mitigation measures X – Non-compliance of mitigation measures N/A – Not applicable

APPENDIX H SUMMARY OF ENVIRONMENTAL LICENSING AND PERMIT STATUS

APPENDIX H – Summary of Environmental Licensing and Permit Status

Permit / License No.	Valid	Period	Details	Status	
Permit / License No.	From To		Details	Status	
Environmental Permi	t (EP)				
EP-265/2007	22/3/2007 N/A		Expansion and upgrading of existing Tai Po Sewage Treatment Works from 100,000 m³/day to 130,000 m³/day: (a) additional secondary treatment process units(1 primary clarified; 3 bioreactors and 2 final clarifiers); (b) reconstruction of 4 existing final clarified; (c) provision of ultraviolet disinfection facilities; (d) additional sludge treatment facilities; and (e) ancillary works to existing treatment facilities.	Valid	
Registration of Chem	ical Waste Pr	oducer			
5517-727-T3270-01		N/A	Major chemical waste types: Spent lubricating oil, spend hydraulic oil, spend cooling oil, surplus paint, spent alkaline electrolyte, spent battery and battery parts containing heavy metals, scrap battery cell containing heavy metals, Nickel and its compounds, spent flammable liquid, spent copper etchant (Ferric chloride), Sodium hypochlorite, polymer, electric and torch bulbs and tubes, alkaline cleaner (spent alkaline solution)	Valid	

APPENDIX I WASTE GENERATION IN THE REPORTING QUARTER Name of Department: Drainage Services Department

Contract No.: DE/2009/09

Monthly Summary - Waste Flow Table for (2012)

		Annual Qua	ntities of Inert C	C&D Materials Ge	nerated Monthly	Annual Quantities of C&D Materials Generated Monthly					
Month	Total Quantity Generated	Hard Rock & Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemicals Waste	Others, e.g. general refuse
	(in m ³)	(in m ³)	(in m ³)	(in m ³)	(in m ³)	(in m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in tonne)
Jan	0	0	0	0	0	0	0	0	0	0	3.9
Feb	0	0	0	0	0	0	0	0	0	0	0
Mar	0	0	0	0	0	0	1.5	0.20	0	0	6.4
Apr	0	0	0	0	0	0	0	0.07	0	0	1.3
May	0	0	0	0	0	0	0	0.15	0	0	4.9
June	0	0	0	0	0	0	17.8	0	0	1030(L)	1.9
July	0	0	0	0	0	0	0	0	0	0	1.3
Aug	0	0	0	0	0	0	0	0.11	0	0	2.3
Sept	0	0	0	0	0	0	0	0.33	0	0	0
Oct											
Nov											
Dec											
Total							19.3	0.86	0	1030(L)	22.0

	Forecast of Total Quantities of C&D Materials to be Generated from the Contractor									
Total Quantity Generated	Hard Rock & Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note 3)	Chemicals Waste	Others, e.g. general refuse
(in m ³)	(in m ³)	(in m ³)	(in m ³)	(in m ³)	(in m ³)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in '000 kg)	(in tonne)
0	Nil	0	0	0	0	100	100	50	10	500

Notes:

The performance targets are given in PS Clause 1.40.8(14).
The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³. (PS Clause 1.40.7(4)(b) refers.

APPENDIX J SUMMARY OF EXCEEDANCE

APPENIDX J – SUMMARY OF EXCEEDANCE

Reporting Month: July to September 2012

- a) Exceedance Report for 1-hr TSP (NIL)
- b) Exceedance Report for 24-hr TSP (NIL)
- c) Exceedance Report for Construction Noise (NIL)

APPENDIX K COMPLAINT LOG

APPENDIX K - COMPLAINT LOG

Reporting Month: July to September 2012

Log Ref.	g Ref. Location Received Date		Details of Complaint	Investigation/Mitigation Action	Status
N/A	N/A	N/A	N/A	N/A	N/A

Remarks: No environmental complaint was received in the reporting month.
