MONTHLY EM&A REPORT

ATAL-Degrémont-China State Joint Venture

Contract No. DC/2008/03
Design, Build and Operate Pillar
Point Sewage Treatment Works:
Fifteenth Monthly EM&A Report

February 2012

Environmental Resources Management

21/F Lincoln House 979 King's Road Taikoo Place Island East, Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

MONTHLY EM&A REPORT

ATAL-Degrémont-China State Joint Venture

Contract No. DC/2008/03 Design, Build and Operate Pillar Point Sewage Treatment Works: Fifteenth Monthly EM&A Report

February 2012 Reference 0119806

For and on behalf of
ERM-Hong Kong, Limited
Approved by: Frank Wan
Signed: Marchine
Position: Partner
Certified by:(Environmental Team Leader – Winnie Ko)
Certified by: (Registered Landscape Architect (R078) - Christina Ip)
Date: 14 February 2012



AECOM 8/F Grand Central Plaza, Tower 2 138 Shatin Rural Committee Road Shatin, Hong Kong www.aecom.com +852 3922 9000 tel +852 3922 9797 fax

Your Ref:

Our Ref:

60017423/C/jwym/12021301

By Hand & By Fax (2833 9162)

Drainage Services Department Sewage Services Branch Harbour Area Treatment Scheme Division 5/F., Western Magistracy, 2A Pok Fu Lam Road, Hong Kong.

Attn: Mr. Kenley C.K. KWOK (T: 2159 3409)

13 February 2012

Dear Sir,

Contract No. DC/2008/03
Design, Build and Operate
Pillar Point Sewage Treatment Works

Monthly EM&A Report for January 2012

Reference is made to Environmental Team (ET)'s draft of the Monthly EM&A Report for January 2012 provided by email dated 8 February 2012. We have no further comment.

We hereby verify the said Monthly EM&A Report as having complied with the requirement as set out in the EM&A Manual in accordance with the condition 3.6 of Environmental Permit No. EP-321/2008.

Should you have any queries, please feel free to contact the undersigned at 3922 9393.

Yours faithfully,

For and on behalf of AECOM Asia Co. Ltd.

Y T Tang

Independent Environmental Checker

c.c. AECOM – Mr. Tim Lee ERM – Ms. Winnie Ko

ATAL-Degremont-China State JV - Mr. C.Y. Fong

(Fax No. 2317 7609)

(Fax No. 2723 5660)

(Fax No. 2811 3321)

CONTENTS

1	INRODUCTION	1
1.1	PURPOSE OF THE REPORT	1
1.2	STRUCTURE OF THE REPORT	1
2	PROJECT INFORMATION	3
2.1	BACKGROUND	3
2.2	GENERAL SITE DESCRIPTION	4
2.3	CONSTRUCTION ACTIVITIES	4
2.4	PROJECT ORGANISATION AND MANAGEMENT STRUCTURE	4
2.5	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	4
3	ENVIRONMENTAL MONITORING REQUIREMENTS	5
3.1	AIR QUALITY MONITORING	5
3.1.1	Monitoring Location	5
3.1.2	Monitoring Parameter and Frequency	5
3.1.3	Action and Limit Levels	5
3.1.4	Monitoring Equipment	5
3.1.5	Monitoring Methodology	6
3.1.6	Event and Action Plan	8
3.2	LANDSCAPE AND VISUAL MONITORING	8
3.3	ENVIRONMENTAL MITIGATION MEASURES AND ENVIRONMENTAL	
	REQUIREMENTS IN CONTRACT	8
4	IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS	S 9
5	MONITORING RESULTS	10
5.1	AIR QUALITY	10
6	WASTE MANAGEMENT	11
7	ENVIRONMENTAL INSPECTIONS	12
7.1	WEEKLY SITE AUDITS	12
7.2	LANDSCAPE AND VISUAL MONITORING	14
8	ENVIRONMENTAL NON-CONFORMANCE	16
8.1.1	Summary of Monitoring Exceedance	16
8.1.2	Summary of Environmental Non-Compliance	16
8.1.3	Summary of Environmental Complaint	16
8.1.4	Summary of Environmental Summon and Successful Prosecution	16
9	FIITURE KEY ISSUES	17

9.1.1 9.1.2 9.1.3	Monitorin	for the Coming Month g Schedule for the Next Reporting Period on Programme for the Next Three Months	17 17 17
10	REVIEW (OF THE EM&A DATA AND EIA PREDICTIONS	18
10.1 10.2 10.3		TY NAGEMENT ON OF REVIEW	18 18 19
11	CONCLUS	SIONS	20
	LIST OF T	ABLES	
Table 2.1 Table 2.2 Table 3.1 Table 3.2 Table 3.3 Table 3.4 Table 6.1 Table 9.1 Table 10.1 Table 10.2	Summary Constructi Constructi Action and TSP Monit Quantities Constructi Compariso Quantity of Wastes Ge	of Construction Activities Undertaken in Reporting Period of Environmental Licensing, Notification and Permit Status on Phase Air Monitoring Locations on Phase Air Quality Monitoring Parameters and Frequency Limit Levels for Air Quality oring Equipment of Waste Generated from the Project on Works to be Undertaken in the Next Reporting Period on of the HKAQO and Air Quality Monitoring Results of Actual Amount of C&D Materials, General Wastes and Chemerated and EIA Estimation	nical
	Annex A	Location of Project	
	Annex B	Works Location	
	Annex C	Project Organization Chart and Contact Detail	
	Annex D	Locations of Air Quality Monitoring Stations	
	Annex E	Monitoring Schedule of the Reporting Month and Next Mon	nth
	Annex F	24-hour and 1-hour TSP Monitoring Results	
	Annex G	Calibration Reports for HVSs	
	Annex H	Event / Action Plan for Air Quality Monitoring	
	Annex I	Implementation Schedule of Mitigation Measures	
	Annex J	Waste Flow Table	
	Annex K	Environmental complaint, Environmental Summons and Prosecution Log	
	Annex L	Construction Programme for the Project	

EXECUTIVE SUMMARY

The construction works of *DC/2008/03 of Design, Build and Operate Pillar Point Sewage Treatment Works (the Project)* commenced on 13 November 2010. This is the 15th monthly Environmental Monitoring and Audit (EM&A) report presenting the EM&A works carried out during the period from 1 to 31 January 2012 in accordance with the EM&A Manual.

Summary of Construction Works undertaken during the Reporting Month

Works undertaken in the reporting month include:

- Drainage pipe work at Admin Building;
- Constructing foundation at Sludge Dewatering Building;
- Excavation at Electrical Building No.1; and
- Constructing wall at P2 CEPT and PTW area.

Environmental Monitoring and Audit Progress

A summary of the monitoring activities undertaken in this reporting period is listed below:

- 24-hour TSP Monitoring at each monitoring station (AM1 and AM2) 5 sets
- 1-hour TSP Monitoring at each monitoring station (AM1 and AM2) 15 sets
- Joint Environmental Site Inspection

4 times

Landscape & Visual Monitoring

once

Air Quality

5 sets of 24-hour TSP and 15 sets of 1-hr TSP measurements were carried out at each of the designated monitoring stations during the reporting period. No exceedance was recorded during the reporting period.

Waste Management

Waste generated from this Project includes inert construction and demolition (C&D) materials (public fill) and non-inert C&D materials (construction wastes). A total of 285 tonnes of public fill were delivered to the fill bank. No plastic and paper/cardboard was recovered and 20 kg of metals were sent to recyclers in the reporting period. 49.01 tonnes general refuse was disposed of in the reporting period. No chemical waste was disposed of in the reporting period.

Environmental Site Inspection

Four weekly joint environmental site inspections were carried out by the representatives of the Contractor, the SOR and the Environmental Team (ET). Details of the audit findings and implementation status of the mitigation measures are presented in *Section 7.1*.

Landscape & Visual

Review on landscape and visual mitigation measures was performed on 27 January 2012. Details of the audit findings and implementation status of the mitigation measures are presented in *Sections 3.2* and 7.2.

Environmental Exceedance/Non-conformance/Compliant/Summons and Prosecution

No exceedance was recorded during the reporting period.

No non-compliance event was recorded during the reporting period.

No environmental complaint and summon/prosecution was received in this reporting period.

Future Key Issues

Works to be undertaken in the next reporting month include:

- Constructing drainage pipe work at Admin Building;
- Constructing foundation at Sludge Dewatering Building;
- Constructing wall and water test at P2 CEPT and PTW area;
- Construction trench and wall at Electrical Building No.1; and
- Excavation at UV Building.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoff, waste management and landscaping issues.

1 INRODUCTION

ERM-Hong Kong, Limited (ERM) was appointed by ATAL – Degrémont – China State Joint Venture (ADC-JV) (the Contractor) as the Environmental Team (ET) to undertake the Environmental Monitoring and Audit (EM&A) programme for the *Contract No. DC/2008/03 of Design, Build and Operate Pillar Point Sewage Treatment Works (the Project)*.

1.1 PURPOSE OF THE REPORT

This is the 15th EM&A report which summarises the impact monitoring results and audit findings for the EM&A programme during the reporting period from 1 to 31 January 2012.

1.2 STRUCTURE OF THE REPORT

The structure of the report is as follows:

Section 1: Introduction

details the scope and structure of the report.

Section 2: **Project Information**

summarises background and scope of the Project, site description, project organization, construction programme, the construction works undertaken and the status of Environmental Permits (EP)/licences over the construction phase of the Project.

Section 3: Environmental Monitoring Requirements

summarises the environmental monitoring including monitoring parameters, monitoring programmes, monitoring methodologies, monitoring frequency, monitoring locations, Action and Limit Levels, Event/Action Plans, environmental mitigation measures as recommended in the approved EIA report, EP and relevant environmental requirements stated in the Contract Specification.

Section 4: **Implementation Status on Environmental Mitigation Measures** summarises the implementation of environmental protection measures during the reporting period.

Section 5: **Monitoring Results**

summarises the monitoring results obtained in the reporting period.

Section 6: Waste Management

summarises the quantity of public fill and construction waste generated in the reporting period

Section 7: **Environmental Site Inspection**

summarises the audit findings of the weekly site inspections undertaken within the reporting period.

Section 8: Environmental Non-conformance

summarises any exceedance of environmental performance standard, and environmental complaints and environmental summons received within the reporting period.

Section 9: Further Key Issues

summarises the impact forecast and monitoring schedule for the next reporting month.

Section 10: Review of the EM&A Data and Predictions

compares the monitoring data and waste quantity against predictions in the approved Project EIA report.

Section 11: Conclusions

2 PROJECT INFORMATION

2.1 BACKGROUND

The existing Pillar Point Sewage Treatment Works (PPSTW) is located to the north of the Tuen Mun River Trade Terminal and is abutting the Lung Mun Road to its north. It is a preliminary treatment works with screening and grit removal processes with treated effluent discharged to the sea (North Western Water Control Zone) via a twin submarine outfall. The *Review of the Tuen Mun and Tsing Yi Sewerage Master Plan* (RTMTYSMP) commissioned in February 1999, recommended to expand the sewage treatment capacity and to upgrade the plant to chemically enhanced primary treatment (CEPT) with disinfection in order to cater for the projected ultimate population and planned developments in the Tuen Mun area, and to improve the effluent quality and hence to reduce pollution loadings to the receiving waters.

The upgrading of the PPSTW comprises the following works:

- expanding the treatment capacity of the existing PPSTW to cope with the increased peak wet-weather sewage flow in Tuen Mun area;
- upgrading the sewage treatment level of the existing PPSTW to incorporate chemical treatment with disinfection at minimum removal rates of 70%, 55% and 99.9% of suspended solids (SS), biochemical oxygen demand (BOD) and *E.coli*, respectively;
- upgrading existing septic waste reception facilities at PPSTW; and
- providing and upgrading ancillary facilities including the administration building, workshop, laboratory, odour control facilities, sludge handling and dewatering facilities, access roads and minor landscaping works within the STW for the operation and maintenance of the upgraded STW.

The potential environmental impacts of the Project have been studied in the "Upgrading of Pillar Point Sewage Treatment Works" (EIAO Register No: AEIAR-145/2008). The EIA was approved on 10 June 2008 under the Environmental Impact Assessment Ordinance (EIAO) and an Environmental Permit (EP-321/2008) for the works was granted on 17 November 2008. Under the requirements of Condition 3.1 of EP-322/2008, an EM&A programme as set out in the EM&A Manual is required to be implemented.

The construction works commenced on 13 November 2010 and are scheduled for completion by 2014.

2.2 GENERAL SITE DESCRIPTION

The open area adjacent to the existing PPSTW has been designated for the upgrading works. The layout of the upgrading works is illustrated in *Annex A*

2.3 CONSTRUCTION ACTIVITIES

A summary of the major construction activities undertaken in the reporting period is shown in *Table 2.1*. The locations of the construction activities are shown in *Annex B*. The construction programme of the Project in the reporting month and the upcoming 3 months is presented in *Annex L*.

Table 2.1 Summary of Construction Activities Undertaken in Reporting Period

Construction Activities Undertaken

- Drainage pipe work at Admin Building;
- Constructing foundation at Sludge Dewatering Building;
- Excavation at Electrical Building No. 1; and
- Constructing wall at P2 CEPT and PTW area.

2.4 PROJECT ORGANISATION AND MANAGEMENT STRUCTURE

The project organization chart and contact details are shown in *Annex C*.

2.5 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the valid permits, licences, and/or notifications on environmental protection for this Project is presented in *Table 2.2*.

Table 2.2 Summary of Environmental Licensing, Notification and Permit Status

Permit/ Licences/	Reference	Validity Period	Remarks
Notification			
Environmental	EP-321/2008	Throughout the	Permit granted on 17
Permit		Contract	November 2008.
Notification of	Ref No. 308136	Throughout the	-
Construction Works		Contract	
under Air Pollution			
Control (Construction			
Dust) Regulation			
Water Discharge	WT00008027-	Till 31 December	Wastewater discharge
License	2010	2015	licence was issued by
			EPD on 7 December 2010.
Construction Noise	GW-RW031-12	28 January 2012 – 27	
Permit		July 2012	-
Chemical Waste	5213-421-A2620-	Throughout the	Licence approved on 28
Producer Registration	01	Contract	October 2010

3.1 AIR QUALITY MONITORING

3.1.1 Monitoring Location

The proposed air quality monitoring stations for the construction phase of the Project, as recommended in the approved EM&A Manual, are given in *Table 3.1* and shown in *Annex D*. The proposed locations (AM1 and AM2) have been agreed with the Drainage Services Department (DSD), Environmental Protection Department (EPD) and the Independent Environmental Checker (IEC).

Table 3.1 Construction Phase Air Monitoring Locations

Monitoring ID	Air Quality Monitoring Station
AM1	Tuen Mun EMSD Servicing Vehicle Station
AM2	River Trade Terminal Office

3.1.2 Monitoring Parameter and Frequency

The construction phase air quality monitoring has been conducted at the designated monitoring stations in accordance with the requirements stipulated in the EM&A Manual. 1-hour and 24-hour TSP levels have been monitored at the frequency and duration stated in *Table 3.2*. The construction phase TSP monitoring has been conducted as per the schedule presented in *Annex E*.

Table 3.2 Construction Phase Air Quality Monitoring Parameters and Frequency

Parameter	Frequency
24-hour TSP	Once every 6 days
1-hour TSP	3 times every 6 days

3.1.3 Action and Limit Levels

The Action and Limit levels have been established and presented in *Table 3.3*.

Table 3.3 Action and Limit Levels for Air Quality

Parameter	Air Monitoring Station	Action Level, µgm-3	Limit Level, µgm-3
24-hour TSP	AM1	183	260
	AM2	192	260
1-hour TSP	AM1	343	500
	AM2	383	500

3.1.4 Monitoring Equipment

Continuous 24-hour and 1-hour TSP monitoring were performed using High Volume Samplers (HVS) with appropriate sampling inlets installed, located at the designated monitoring stations.

The performance specification of HVS complied with the standard method "Determination of Suspended Particulate Matter in the Atmosphere (High Volume Method)" as stipulated in US EPA Standard Title 40, Code of Federation Regulations Chapter 1 (Part 50 Appendix B). Table 3.4 summarises the equipment that were deployed for the 24-hour and 1-hour TSP monitoring respectively.

Table 3.4 TSP Monitoring Equipment

Monitoring Station	Monitoring Equipment (HVS and Calibrator)
24-hr and 1-hr TSP	
AM1	GMW GS-2310 (S/N 7580), CM-AIR-43 (S/N 9833620)
AM2	GMW GS-2310 (S/N 1252), CM-AIR-43 (S/N 9833620)

3.1.5 Monitoring Methodology

The setup locations of the HVSs at monitoring stations were listed in *Table 3.1*. All HVSs were free-standing with no obstruction.

The following criteria were considered in the installation of the HVSs:

- appropriate support to secure the samplers against gusty wind were provided at AM1 and AM2;
- a minimum of 2m separation from walls, parapets and penthouses was required for rooftop samplers;
- no furnace or incinerator flues were nearby;
- airflow around the sampler was unrestricted; and
- permission was obtained to set up the samplers and to gain access to the monitoring stations.

Preparation of Filter Papers

- glass fibre filters were labelled and sufficient filters that were clean and without pinholes were selected;
- all filters were equilibrated in the conditioning environment for 24 hours before weighing. The conditioning environment temperature was around 25°C and not variable by more than ± 3°C; the relative humidity (RH) was 40%; and
- SGS Hong Kong Ltd, a HOKLAS accredited laboratory, implements comprehensive quality assurance and quality control programmes.

Field Monitoring

• the power supply was checked to ensure that the HVSs were working properly;

- the filter holder and the area surrounding the filter were cleaned;
- the filter holder was removed by loosening the foul bolts and a new filter, with stamped number upward, on a supporting screen was aligned carefully;
- the filter was properly aligned on the screen so that the gasket formed an airtight seal on the outer edges of the filter;
- the swing bolts were fastened to hold the filter holder down to the frame. The pressure applied should be sufficient to avoid air leakage at the edges;
- then the shelter lid was closed and secured with the aluminium strip;
- the HVSs were warmed-up for about 5 minutes to establish runtemperature conditions;
- a new flowrate record sheet was set into the flow recorder;
- the flow rates of the HVSs were checked and adjusted to between 1.22 1.37 m³min⁻¹ which were within the range specified in the EM&A Manual (ie 0.6 1.7 m³min⁻¹);
- the programmable timer was set for a sampling period of 24 hours ± 1 hour, and the starting time, weather condition and the filter number were recorded;
- the initial elapsed time was recorded;
- at the end of sampling, the sampled filter was removed carefully and folder in half length so that only surfaces with collected particulate matter were in contact:
- it was then placed in a clean plastic envelope and sealed;
- all monitoring information was recorded on a standard data sheet; and
- filters were sent to SGS Hong Kong Ltd for analysis.

Maintenance and Calibration

- the HVSs and their accessories were maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply; and
- the flow rate of each HVS with mass flow controller were calibrated using an orifice calibrator. Initial calibrations of the dust monitoring equipments were conducted upon installation and prior to commissioning. Five-point calibration was carried out for HVSs using CM-AIR-43 Calibration Kit. HVSs are calibrated on a bi-monthly basis. The calibration records for the HVSs are given in *Annex G*.

Wind Data Monitoring

Average wind data (wind speed and wind direction) during the monitoring period were obtained from the meteorological station at Tuen Mun of the Hong Kong Observatory (HKO) and were presented in *Annex F*.

3.1.6 Event and Action Plan

The Event/Action Plan (EAP) for air quality monitoring is presented in *Annex H*.

3.2 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, monthly landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures recommended in the approved EIA Report are fully achieved. The monitoring procedures and criteria as described in the EM&A Manual were adopted.

3.3 ENVIRONMENTAL MITIGATION MEASURES AND ENVIRONMENTAL REQUIREMENTS IN CONTRACT

All relevant environmental mitigation measures listed in the EIA Report and the EM&A Manual as well as the specific environmental requirements stated in Contract Specification are summarised in *Annex I*. A summary of the key environmental mitigation measures implemented as per the Contract Requirements is also presented in *Annex I*.

4 IMPLEMENTATION STATUS ON ENVIRONMENTAL PROTECTION REQUIREMENTS

The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Report, EM&A Manual and EP. The implementation status of the measures during the reporting period is summarised in *Annex I*.

5 MONITORING RESULTS

5.1 AIR QUALITY

A total of 5 sets of 24-hour and 15 sets of 1-hour TSP measurements have been taken at each of the monitoring stations (AM1 and AM2) during the reporting period. The monitoring data for 24-hour TSP and 1-hour TSP together with wind data and graphical presentations for the past 4 months are presented in *Annex F*. The weather conditions during the monitoring period ranged from Cloudy to Sunny. The local impacts near the monitoring stations of AM1 and AM2 were mainly associated with vehicular emissions. No exceedance of Action and Limit Level of 1-hr and 24-hr TSP was recorded during the reporting period.

Wastes generated from this Project include inert construction and demolition (C&D) materials (public fill) and non-inert C&D materials (construction waste). Construction waste comprises of general refuse, metals and paper/cardboard packaging materials. Metals generated from the Project are also grouped into construction waste as the materials were not disposed of with others at public fill. Reference has been made to the Monthly Summary Waste Flow Table prepared by the Contractor (*Annex J*). With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting month are summarised in *Table 6.1* below. The public fill and construction waste generated from the Project have been disposed of at the Tuen Mun Area 38 Fill Bank and WENT Landfill, respectively. No plastic and paper/ cardboard packing was sent to recyclers for recycling during the reporting period. However, 20 kg of metals were sent to recyclers for recycling during the reporting period.

Table 6.1 Quantities of Waste Generated from the Project

Month / Year Quantity			
	C&D Materials Disposed	C&D Materials Disposed of at	Chemical
	of at Public Fill (inert) (a)	Landfill (Non-inert)	Waste ^(d)
		(Construction waste) (b) (c)	
January 2012	285 tonnes	49.01 tonnes	0 L

Notes:

- (a) Inert C&D materials (public fill) include bricks, concrete, building debris, rubble and excavated soil. Total 285 tonnes of public fill were generated and were disposed of at the Tuen Mun Area 38 Fill Bank.
- (b) Non-inert C&D materials (construction wastes) include metals, paper / cardboard packaging waste, plastics and other wastes such as general refuse. Metals generated from the Project are grouped into construction wastes as the materials were not disposed of with others at the public fill. 49.01 tonnes of general refuse is recorded in the reporting month. Construction wastes other than metals and paper/cardboard packaging were disposed of at WENT Landfill. No plastic and paper/cardboard packaging was recovered and 20 kg of metals were recovered and sent to recyclers for recycling during the reporting period.
- (c) General refuse was disposed of at WENT by subcontractors.
- (d) Chemical waste was collected though the licensed chemical waste collector, Dunwell Ind. (Holdings) Ltd, with the waste collection licence number 7111-757-W0015-WC.

7

7.1 WEEKLY SITE AUDITS

Joint site inspections were conducted by representatives of the Contractor, SOR and the ET on 6, 16 and 27 January 2012. A joint site inspection was conducted by representatives of Contractor, SOR and IEC was the joint inspection on 11 January 2012 and a site inspection was conducted by representatives of the Contractor and ET on 12 January 2012. There was no non-compliance recorded during the site inspections.

Major observations during the reporting period were summarised as follows:

6 January 2012

- Environmental permit was missing at the entrance of P2 worksite. The Contractor was reminded to display the environmental permit immediately.
- Muddy water was observed discharging into the storm drain next to sludge dewatering building worksite. The discharged water was muddy although had been treated by sedimentation tanks. The Contractor was reminded to stop discharging the muddy water and was reminded to clean-up the channel immediately. The Contractor was also reminded to review the capacity of the sedimentation tank and remove the sediment inside the tank. The Contractor was also reminded to provide proper sedimentation tank with sufficient treatment capacity to ensure the effluent quality are in compliance of the effluent discharge permit before discharging within 3 working days.
- Retained trees 150 and 148 near Gate 3 at P2 site area were observed damaged. The Contractor was reminded to provide proper instruction and training for the workers to remind the works to avoid damaging retained trees especially during lifting works.
- Oil stain was observed under the crane truck near Gate 2. The Contractor was reminded to remove the oil stain and to provide proper maintenance to the crane truck to avoid leakage of hydraulic oil within 3 working days.
- Stagnant water with moss and general refuse was observed at wheel washing bay near Gate 3. The Contractor was reminded to clean-up the wheel washing bay within 3 working days.
- Chemical tanks without drip tray and oil stains were observed in Metal Storage Area. The Contractor was reminded to provide drip tray for the chemical drum and remove the oil stains within 3 working days.
- Exposed soil surface and earth stockpile were observed at Stockpiling Area. The Contractor was reminded to properly cover the exposed soil surface and earth stockpile within 3 working days.

11 January 2012

- Accumulation of leaves and debris were observed inside the U-channels along the site boundaries. The Contractor was recommended to clear the accumulated leaves and debris and conduct regular maintenance of drainage channels within the works areas.
- Exposed soil surfaces at stockpile area were found loosely covered up with tarpaulin sheet. The Contractor was recommended to provide tarpaulin sheet coverage to the exposed soil surfaces to minimize the dust impacts.

12 January 2012

- Exposed soil surface and earth stockpile were observed at Stockpiling Area. The Contractor was reminded to properly cover the exposed soil surface and earth stockpile within 3 working days.
- General refuses were observed inside the surface drainage channel. The Contractor was reminded to remove the refuses within 3 working days.
- Construction material and general refuse was observed inside the tree protection zone of retained tree no. 143. Also a fencing of the tree protection zone for retained tree no. 148 was observed missing. The Contractor was reminded to remove the construction material and general refuses and provide fencing for the tree protection zone within 3 working days in order to protect the trees.
- The pump for pumping away stagnant water at the concreted pit at CEPT work site was observed not operating. The Contractor was reminded to switch on the pump ASAP in order to prevent accumulation of stagnant water.

16 January 2012

- General refuses and stagnant water were observed inside concreted pit, wheel washing bay and the surface drainage channel at P2 CEPT work site. The Contractor was reminded to remove the stagnant water and general refuses within 3 working days.
- Construction material and general refuse was observed inside the tree protection zone of retained tree no. 143. Also a fencing of the tree protection zone for retained tree no. 148 was observed missing. The Contractor was reminded to remove the construction material and general refuses and provide proper tree protection zone fencing for the retained trees within 3 working days in order to protect the trees.
- The pump for pumping away stagnant water at the concreted pit at CEPT work site was observed not operating. The Contractor was reminded to switch on the pump immediately in order to prevent accumulation of stagnant water.
- Stagnant water was observed inside the drainage channel. The Contractor was reminded to remove the stagnant water within 3 working days and also recommended to investigate any blockage inside the drainage channel.

27 January 2012

- Oily water was observed in drip tray at P2 near sludge dewatering building. The Contractor was reminded to remove the oily water within 3 working days and dispose of as chemical waste via licensed chemical waste collector.
- Stagnant water was observed on floor at P2 near Gate 3. The Contractor was reminded to remove the stagnant water within 3 working days.
- General refuse and stagnant water was observed in some concreted pit at CEPT work site. The Contractor was reminded to remove the general refuses and stagnant water within 3 working days.

Follow-up actions were undertaken as reported by the Contractor and observed in the next weekly site inspections conducted in the reporting period.

7.2 LANDSCAPE AND VISUAL MONITORING

In accordance with the EM&A Manual, monthly landscape and visual monitoring is required to ensure that the design, implementation and maintenance of landscape and visual mitigation measures recommended in the EIA Report are fully achieved. A review of landscape and visual mitigation measures was performed on 27 January 2012. It was confirmed that most of the necessary landscape and visual mitigation measures as summarised in *Annex I* were implemented by the Contractor. The major findings were summarised as follow:

27 January 2012

- Transplanted tree no. 434 (Melia azedarach) at T1 was observed in poor health condition. The Contractor was recommended that it to be inspected by the Contractor's certified arborist ASAP and remediation actions should be undertaken as per the arborist's recommendation.
- Transplanted tree no. 123 and 124 (Hibiscus tiliaceus) at T1 were found to be infected by diseases. The Contractor was recommended that it to be inspected by the Contractor's certified arborist ASAP and remediation actions should be undertaken as per the arborist's recommendation to avoid spreading of the disease.
- Crack was observed on transplanted tree no. 155 (Macaranga tanarius) at T1. The Contractor was recommended that it to be inspected by the Contractor's certified arborist ASAP and remediation actions should be undertaken as per the arborist's recommendation.
- Transplanted tree no. N78 (Melia azedarach) at P2 which was preparing to be transplanted was observed in poor health condition. It was observed no leave on the branches. The Contractor was recommended to closely monitor the health of the tree during transplantation.
- Retained tree no. R69 (Bombax ceiba) at P2 was observed in poor health condition. Only main trunk remained with few water sprouts. The Contractor was recommended that it to be inspected by the Contractor's

- certified arborist ASAP and remediation actions should be undertaken as per the arborist's recommendation.
- It was found that the tree tags for retained tree no. R69 was inconsistence with tree survey report done in September 2010. According to the report, retained tree no. R69 should be Hibiscus tiliaceus, however it was Bombax ceiba during the site inspection. The Contractor was reminded to check and provide suitable tree tag for the retained tree within 3 working days.

The Contractor was reminded to implement the follow-up actions and that the status of the follow-up actions will be reviewed in the first weekly site inspections in the next reporting period.

Key landscape and visual mitigation measures implemented in the reporting period include:

- Set up of a temporary tree nursery;
- Control dust and erosion of exposed soil;
- Stockpiling of topsoil for future reuse;
- Maintain existing tree record inventory; and
- Re-use existing top soil for new planting areas.

8 ENVIRONMENTAL NON-CONFORMANCE

8.1.1 Summary of Monitoring Exceedance

No exceedances of Action and Limit Levels of 1-hr and 24-hr TSP were recorded during the reporting period.

8.1.2 Summary of Environmental Non-Compliance

No non-compliance event was recorded during the reporting period.

8.1.3 Summary of Environmental Complaint

No complaint was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex K*.

8.1.4 Summary of Environmental Summon and Successful Prosecution

No summon was received during the reporting period. The cumulative summons/prosecution log is shown in *Annex K*.

9 FUTURE KEY ISSUES

9.1.1 Key Issues for the Coming Month

Works to be undertaken for the coming monitoring period are summarised in *Table 9.1* below.

Table 9.1 Construction Works to be Undertaken in the Next Reporting Period

Work to be taken

- Drainage pipe work at Admin Building;
- Constructing foundation at Sludge Dewatering Building;
- Constructing walls and water test at P2 CEPT and PTW area;
- Excavation at UV building; and
- Constructing trench and wall at Electrical Building No.1.

Potential environmental impacts arising from the above construction activities will mainly be associated with dust, construction noise, site runoff, waste management and landscaping issues.

9.1.2 Monitoring Schedule for the Next Reporting Period

The tentative schedule of TSP monitoring for the next reporting period was presented in *Annex E*. Environmental monitoring will be conducted at the same monitoring locations in the next reporting period. The monitoring programme has been reviewed and was considered adequate to cater for the nature of works in progress.

9.1.3 Construction Programme for the Next Three Months

The most updated construction programme for the Project is presented in *Annex L*.

10.1 AIR QUALITY

Since the EIA has included only qualitative assessment of dust impact during construction phase, a comparison was made between the monitoring results from the start of the Project and the Hong Kong Air Quality Objectives (HKAQO) (*Table 10.1*).

Table 10.1 Comparison of the HKAQO and Air Quality Monitoring Results

Monitoring Station	HKAQO, ugm ⁻³	Measured 24-hour TSP Monitoring Results, ugm ^{-3 (a) (b)}	
	24 hour (1)	Average	Range
AM1	260	73	59 - 100
AM2	260	81	60 - 102

Notes:

- (a) Only 24-hour TSP monitoring results were compared as there is no 1 hour TSP criterion in HKAQO.
- (b) Average and range of data were calculated between the commencement of construction works and this reporting month.

The monitoring results show that the average and range of 24-hour TSP levels recorded since the commencement of the construction works have been well below the 24-hour TSP criterion in the HKAQO. Recommended mitigation measures in *Section 3.7.1.1* of EIA have been implemented throughout the construction period and were considered effective.

10.2 WASTE MANAGEMENT

The estimated amount of waste generated in this Project and the accumulated quantities of waste generated up to this reporting month are presented in *Table 10.2*. The amount of inert C&D material sent to public fills is larger than the estimated amount in EIA. With reference to the C&D Material Assessment (Contractor's General Submission (CSF) No.:

DC200803/CSF/SAF/060026/A), the difference in quantity is mainly due to differences in excavation depths and excavation methods in the Contract Works and that assumed in the Reference Design. Recommended mitigation measures in *Sections 7.5.1.1* to *7.5.1.9* of the EIA will continue to be implemented during the construction stage.

Table 10.2 Quantity of Actual Amount of C&D Materials, General Wastes and Chemical Wastes Generated and EIA Estimation

Type of Material	Estimated Amount of Public Fill and Construction Waste in EIA (inert & non-inert)	Estimated Amount of Public Fill and Construction Waste in C&D Material Assessment (CSF No.: DC200803/CSF/SAF/0 60026/A) (c)	Amount of Public Fill and Construction Waste Recorded (a) (b)
Amount of C&D	61,489 m ³	77,600 m ³	85,008 m ³
Materials Arising			
Amount of C&D	-	-	$3,164 \text{ m}^3$
Materials Reused on			
other site			
Amount of C&D	14,926 m ³	18,000 m ³	0 m^3
Materials Reused on			
site			
Amount of C&D	46,563m ³	59,600 m ³	81,844 m ³
Materials Sent to			
Public Fills			
General Refuse	Small	-	285.62 tonnes
Chemical Waste	Small	-	810 L

Notes:

- (a) The actual amount of C&D Materials was recorded since the commencement of construction works
- (b) The density of soil and rock (bulked) is 1.8 tonnes/m³.
- (c) The estimated amount of C&D material generated from the Contract Works was revised in the C&D Material Assessment and submitted to the SO on 9 September 2010 (CSF No.: DC200803/CSF/SAF/060026/A) due to the new plant & facility layout.
- (d) The waste flow data for April and May 2011 was updated in August 2011 based on SOR's comments and has been confirmed by the Contractor. The waste flow data for August, September and November 2011 was updated in October, November and December 2011 respectively based on Contractor's revised waste flow summary. Detail of changes is shown in Annex J.

10.3 CONCLUSION OF REVIEW

The EIA predictions and the monitoring results since the commencement of construction works have been reviewed. The EIA concluded that the Project would not cause adverse impacts to the environment, and the monitoring results have also indicated the same so far. Mitigation measures recommended in the EP, EIA and EM&A Manual will continue to be implemented throughout the construction phase of the Project.

11 CONCLUSIONS

This EM&A Report presents the EM&A programme undertaken during the reporting period from 1 to 31 January 2012 in accordance with EM&A Manual and requirements of EP (EP-321/2008).

No exceedance of Action and Limit Levels of 24-hour TSP and 1-hour TSP was recorded at the monitoring stations during the reporting period.

Monthly landscape and visual monitoring was conducted in the reporting period. Most of the necessary landscape and visual mitigation measures recommended in the EIA Report were implemented by the Contractor. Follow-up actions are required by the Contractor to improve protection measures on the retained or to-be transplanted trees.


No non-compliance event was recorded during the reporting period.

No complaint and summons/prosecution was received during the reporting period.

The ET will keep track of the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures in the coming periods.

Annex A

Location of Project

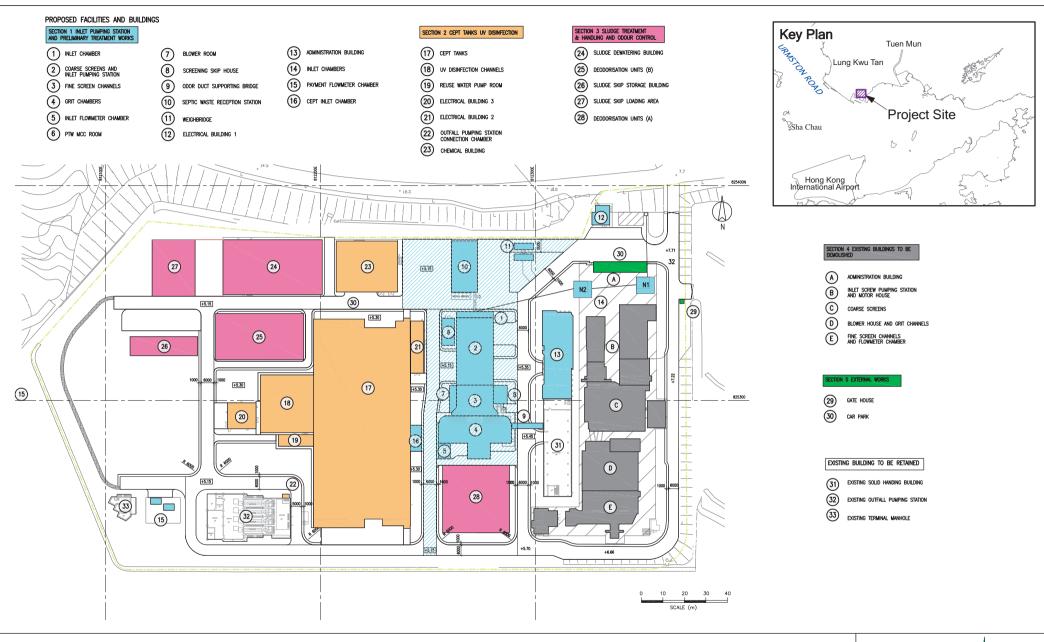

Annex A


Contract No. DC/2008/03 - Design, Build and Operate Pillar Point Sewage Treatment Works Layout of Project

Environmental Resources Management



Annex B


Works Location

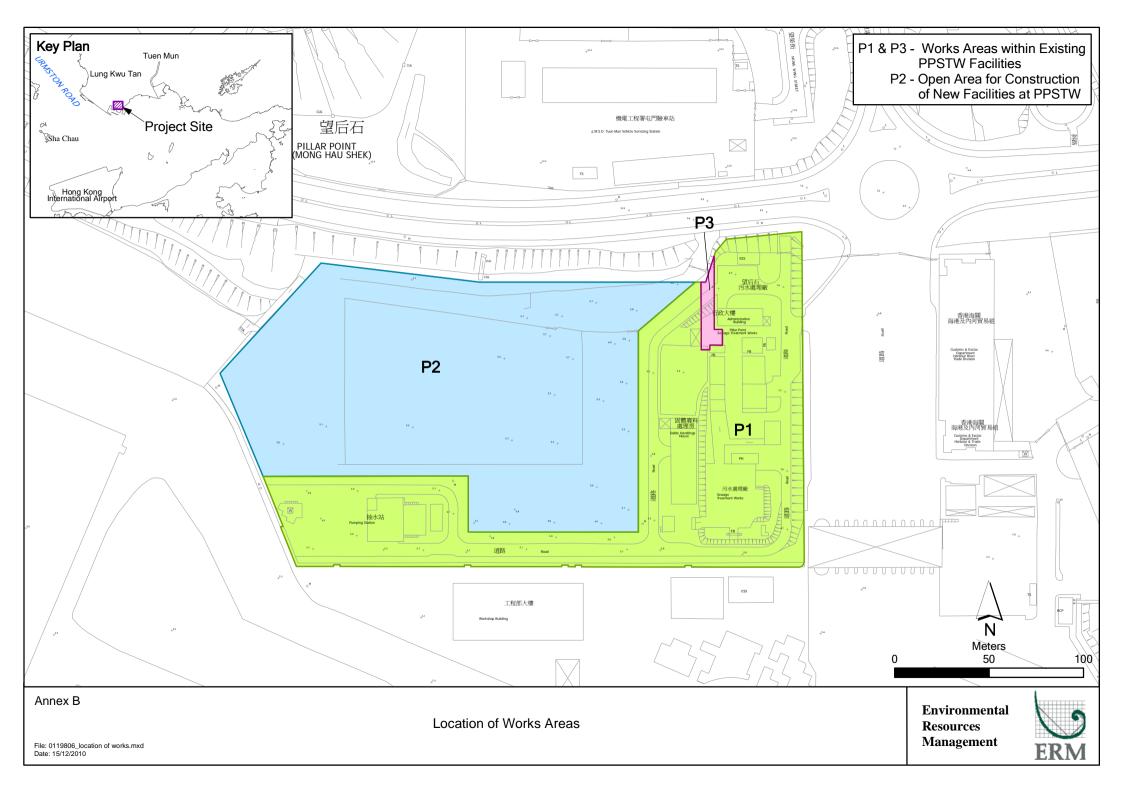

Annex C

Project Organization Chart with Contact Details


Project Organization During Construction Phase (with contact details)

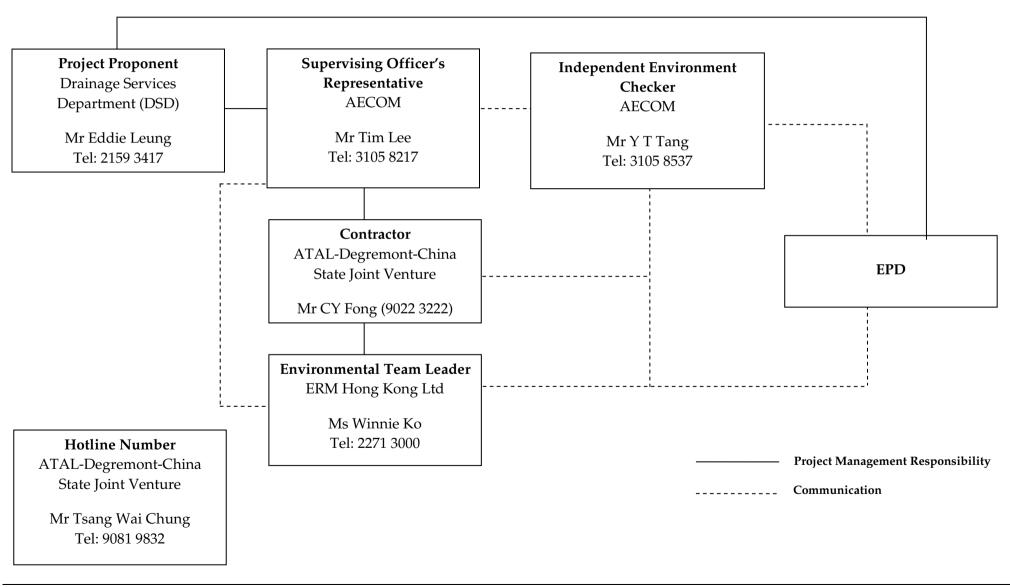

ENVIRONMENTAL RESOURCES MANAGEMENT

Annex D

Locations of Air Quality Monitoring Stations

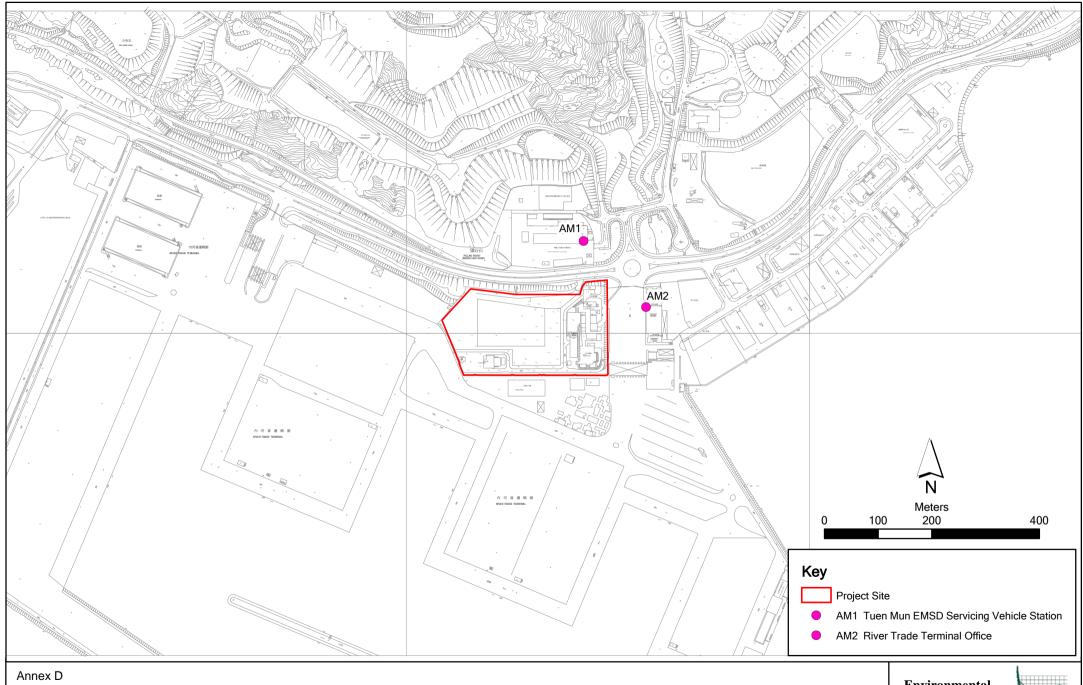

Contract No. DC/2008/03 Design, Build and Operate of Pillar Point Sewage Treatment Works

Environmental Resources Management





AM1 – Tuen Mun EMSD Servicing Vehicle Station



AM2 - River Trade Terminal Office

Annex E

Monitoring Schedule of Reporting Month and Next Month

Contract No. DC/2008/03 - Design, Build and Operate Pillar Point Sewage Treatment Works (Tuen Mun EMSD Servicing Vehicle Station - AM1 & River Trade Terminal Office - AM2) January 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
01-Jan	02-Jan	03-Jan	04-Jan	05-Jan	06-Jan	07-Jan
				3X1-hr & 1X 24-hr TSP		
08-Jan	09-Jan	10-Jan	11-Jan	12-Jan	13-Jan	14-Jan
			3X1-hr & 1X 24-hr TSP			
15-Jan	16-Jan	17-Jan	18-Jan	19-Jan	20-Jan	21-Jan
		3X1-hr & 1X 24-hr TSP				
22-Jan	23-Jan	24-Jan	25-Jan	26-Jan	27-Jan	28-Jan
	3X1-hr & 1X 24-hr TSP				3X1-hr & 1X 24-hr TSP	
29-Jan	30-Jan	31-Jan				

Contract No. DC/2008/03 - Design, Build and Operate Pillar Point Sewage Treatment Works (Tuen Mun EMSD Servicing Vehicle Station - AM1 & River Trade Terminal Office - AM2) February 2012

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		·	01-Feb	02-Feb	03-Feb	04-Feb
				3X1-hr & 1X 24-hr TSP		
				3.11-111 & 1.7.24-111 1.5.5		
05-Feb	06-Feb	07-Feb	08-Feb	09-Feb	10-Feb	11-Feb
			3X1-hr & 1X 24-hr TSP			
12-Feb	13-Feb	14-Feb	15-Feb	16-Feb	17-Feb	18-Feb
		3X1-hr & 1X 24-hr TSP				
19-Feb	20-Feb	21-Feb	22-Feb	23-Feb	24-Feb	25-Feb
	3X1-hr & 1X 24-hr TSP					3X1-hr & 1X 24-hr TSP
26-Feb	27-Feb	28-Feb				

Annex F

24-hour and 1-hour TSP Monitoring Results

Annex F - 24-hour and 1-hour TSP Monitoring Results

1-hour TSP Monitoring Results

Station AM1

				TSP					Wind Speed		
	Start	Finish	Weather	Concentration	Action Level	Limit Level	Site Conditions /	Temperature	*	Sampler	Filter
Date	Time	Time		(μg/m ³)	(µg/m³)	(µg/m³)	Observations / Remarks	(℃)	(m/s)	ID	ID
05-Jan-12	13:10	14:10	Cloudy	121	343	500	Construction work in progress	11.5	*	7580	3256
05-Jan-12	14:10	15:10	Cloudy	125	343	500	Construction work in progress	12	*	7580	3257
05-Jan-12	15:10	16:10	Cloudy	121	343	500	Construction work in progress	12	*	7580	3258
11-Jan-12	13:10	14:10	Cloudy	121	343	500	Construction work in progress	17	*	7580	3339
11-Jan-12	14:10	15:10	Cloudy	125	343	500	Construction work in progress	16.5	*	7580	3340
11-Jan-12	15:10	16:10	Cloudy	124	343	500	Construction work in progress	16	*	7580	3341
17-Jan-12	13:10	14:10	Sunny	120	343	500	Construction work in progress	17.5	*	7580	3347
17-Jan-12	14:10	15:10	Sunny	122	343	500	Construction work in progress	18	*	7580	3429
17-Jan-12	15:10	16:10	Sunny	105	343	500	Construction work in progress	18.5	*	7580	3430
21-Jan-12	13:10	14:10	Cloudy	147	343	500	Construction work in progress	17	*	7580	3445
21-Jan-12	14:10	15:10	Cloudy	161	343	500	Construction work in progress	17	*	7580	3446
21-Jan-12	15:10	16:10	Cloudy	161	343	500	Construction work in progress	17	*	7580	3447
27-Jan-12	13:10	14:10	Cloudy	101	343	500	Construction work in progress	15	*	7580	3462
27-Jan-12	14:10	15:10	Cloudy	120	343	500	Construction work in progress	15	*	7580	3463
27-Jan-12	15:10	16:10	Cloudy	106	343	500	Construction work in progress	15	*	7580	3464
•	•		Min.	101		•		-			

* Wind Speed data is presented in the Meteorological Data table

Max. Average 161

125

Annex F - 24-hour and 1-hour TSP Monitoring Results

1-hour TSP Monitoring Results

Station AM2

				TSP					Wind Speed		
	Start	Finish	Weather	Concentration	Action Level	Limit Level	Site Conditions /	Temperature	*	Sampler	Filter
Date	Time	Time		(μg/m ³)	(µg/m³)	(μg/m³)	Observations / Remarks	(℃)	(m/s)	ID	ID
05-Jan-12	13:00	14:00	Cloudy	119	383	500	Construction work in progress	11.5	*	1252	3252
05-Jan-12	14:00	15:00	Cloudy	127	383	500	Construction work in progress	12	*	1252	3253
05-Jan-12	15:00	16:00	Cloudy	122	383	500	Construction work in progress	12	*	1252	3254
11-Jan-12	13:00	14:00	Cloudy	130	343	500	Construction work in progress	17	*	1252	3335
11-Jan-12	14:00	15:00	Cloudy	136	343	500	Construction work in progress	16.5	*	1252	3336
11-Jan-12	15:00	16:00	Cloudy	121	343	500	Construction work in progress	16	*	1252	3337
17-Jan-12	13:00	14:00	Sunny	103	383	500	Construction work in progress	17.5	*	1252	3346
17-Jan-12	14:00	15:00	Sunny	115	383	500	Construction work in progress	18	*	1252	3426
17-Jan-12	15:00	16:00	Sunny	126	383	500	Construction work in progress	18.5	*	1252	3427
21-Jan-12	13:00	14:00	Cloudy	122	383	500	Construction work in progress	17	*	1252	3441
21-Jan-12	14:00	15:00	Cloudy	108	383	500	Construction work in progress	17	*	1252	3442
21-Jan-12	15:00	16:00	Cloudy	122	383	500	Construction work in progress	17	*	1252	3443
27-Jan-12	13:00	14:00	Cloudy	99	383	500	Construction work in progress	15	*	1252	3458
27-Jan-12	14:00	15:00	Cloudy	92	383	500	Construction work in progress	15	*	1252	3459
27-Jan-12	15:00	16:00	Cloudy	111	383	500	Construction work in progress	15	*	1252	3460
			Min	92		•			·		

Min. 92

Max. 136

Average 117

^{*} Wind Speed data is presented in the Meteorological Data table

Annex F - 24-hour and 1-hour TSP Monitoring Results

24-hour TSP Monitoring Results

Station AM1

Start		Finis	h	Weather	Filter V	Veight (g)	Elapse Read		Sampling Time		r Rate (m	n³/min)	TSP Conc.	Action Level	Limit Level	Observations / Remarks	Sampler	Filter
Date	Time	Date	Time		Initial	Final	Initial	Final	(hrs)	Initial	Final	Average	(μg/m ³)	$(\mu g/m^3)$	(μg/m ³)		ID	ID
05-Jan-12	16:10	06-Jan-12	16:10	Cloudy	2.7463	2.8599	12143.18	12167.18	24.00	1.24	1.24	1.24	64	183	260	Construction work in progress	7580	3259
11-Jan-12	16:10	12-Jan-12	16:10	Cloudy	2.6908	2.8175	12170.18	12194.18	24.00	1.24	1.24	1.24	71	183	260	Construction work in progress	7580	3342
17-Jan-12	16:10	18-Jan-12	16:10	Sunny	2.7149	2.8308	12197.18	12221.18	24.00	1.24	1.24	1.24	65	183	260	Construction work in progress	7580	3431
21-Jan-12	16:10	22-Jan-12	16:10	Cloudy	2.7336	2.8800	12224.18	12248.18	24.00	1.24	1.24	1.24	82	183	260	Construction work in progress	7580	3448
27-Jan-12	16:10	28-Jan-12	16:10	Cloudy	2.7359	2.8750	12251.18	12275.18	24.00	1.24	1.24	1.24	78	183	260	Construction work in progress	7580	3465

Min. 64

Max. 82

Average 72

24-hour TSP Monitoring Results

Station AM2


Start		Finis	h	Weather	Filter W	Veight (g)	Elapse Read		Sampling Time		Rate (m	³ /min)	TSP Conc.	Action Level	Limit Level	Observations / Remarks	Sampler	Filter
Date	Time		Time		Initial	Final	Initial	Final	(hrs)	Initial	Final	Average		(μg/m³)		Observations / Hemaiks	ID	ID
05-Jan-12	16:00	06-Jan-12	16:00	Cloudy	2.7614	2.8992	20160.20	20184.20	24.00	1.23	1.23	1.23	78	192	260	Construction work in progress	1252	3255
11-Jan-12	16:00	12-Jan-12	16:00	Cloudy	2.6857	2.8206	20187.20	20211.20	24.00	1.23	1.23	1.23	76	192	260	Construction work in progress	1252	3338
17-Jan-12	16:00	18-Jan-12	16:00	Sunny	2.6997	2.8249	20214.20	20238.20	24.00	1.23	1.23	1.23	71	192	260	Construction work in progress	1252	3428
21-Jan-12	16:00	22-Jan-12	16:00	Cloudy	2.7004	2.8600	20241.20	20265.20	24.00	1.23	1.23	1.23	90	192	260	Construction work in progress	1252	3444
27-Jan-12	16:00	28-Jan-12	16:00	Cloudy	2.7179	2.8600	20268.20	20292.20	24.00	1.23	1.23	1.23	80	192	260	Construction work in progress	1252	3461

Min. 71 Max. 90 Average 79

Meteorological Data Extracted from the Hong Kong Observatory


			Т	uen Mun Station		
Date	Weather	Average Air Temperature (°C)	Average Relative Humiditiy (%)	Total Rainfall (mm)	Average Wind Speed (km/h)	Wind Direction
05-01-2012	Cloudy	9.1	71 - 90	0.8	15.0	N
06-01-2012	Cloudy	10.8	74 - 95	0.5	15.0	N
11-01-2012	Cloudy	15.8	64 - 80	0.4	10.5	N
12-01-2012	Cloudy	14.4	71 - 93	0.9	9.0	N
17-01-2012	Sunny	16.6	67 - 86	0.0	11.0	N
18-01-2012	Sunny	18.2	75 - 90	0.0	8.0	SW
21-01-2012	Cloudy	17.0	83 - 91	Trace	12.0	N
22-01-2012	Cloudy	13.0	79 - 93	Trace	10.5	SW
27-01-2012	Cloudy	12.9	88 - 92	0.0	7.0	N
28-01-2012	Cloudy	17.6	72 - 94	0.0	3.5	N

1-hr TSP Levels for the Past 4 Months AM1 (Tuen Mun EMSD Vehicle Servicing Station)

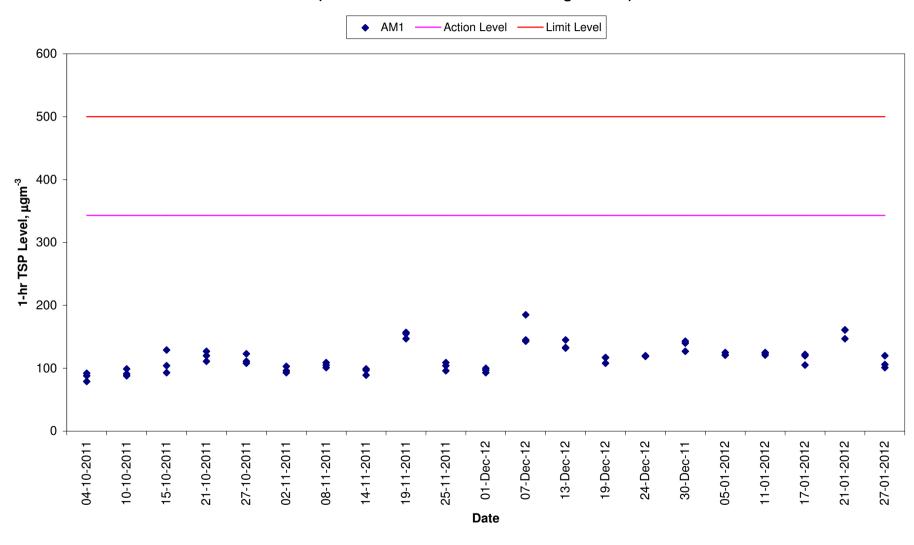


Annex F TSP Monitoring Results

1-hr TSP Levels for the Past 4 Months AM2 (River Trade Terminal Office)

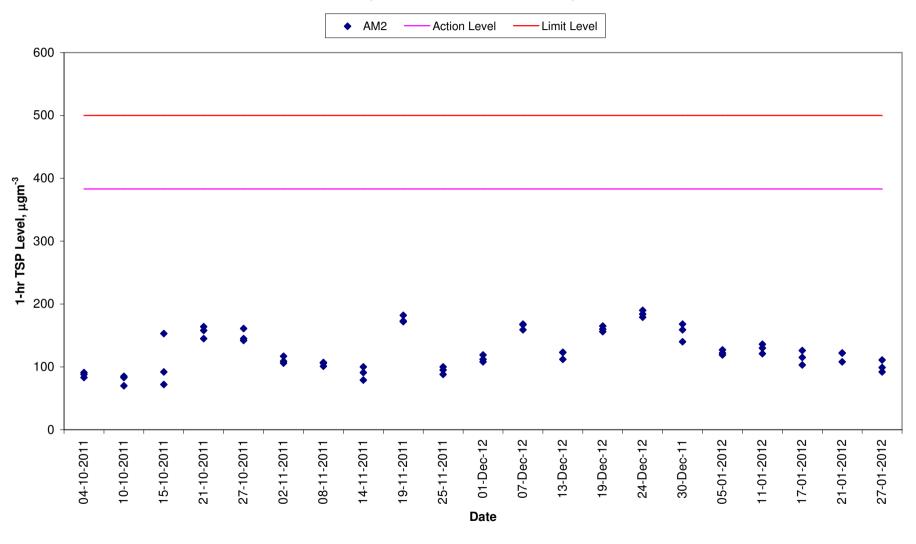


Annex F TSP Monitoring Results

24-hr TSP Levels for the Past 4 Months AM2 (River Trade Terminal Office)

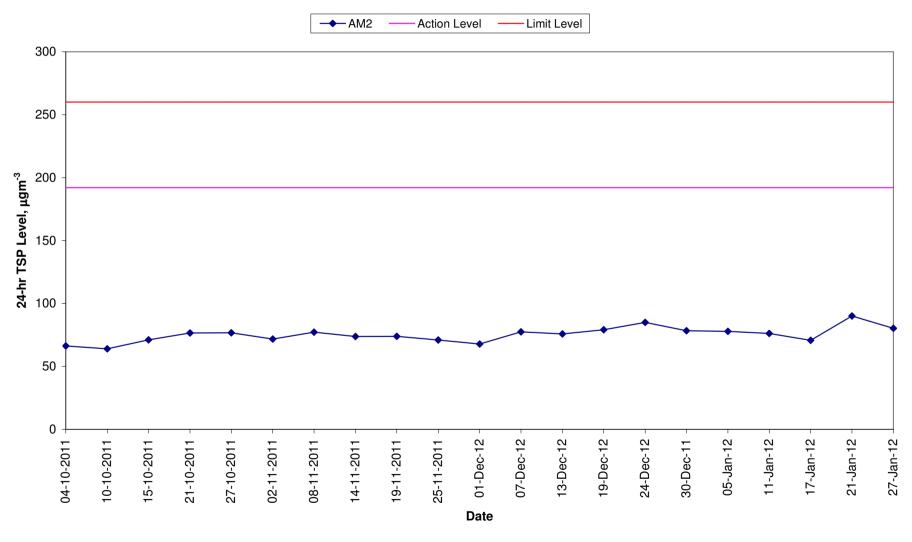

Annex F TSP Monitoring Results

24-hr TSP Levels for the Past 4 Months AM1 (Tuen Mun EMSD Vehicle Servicing Station)

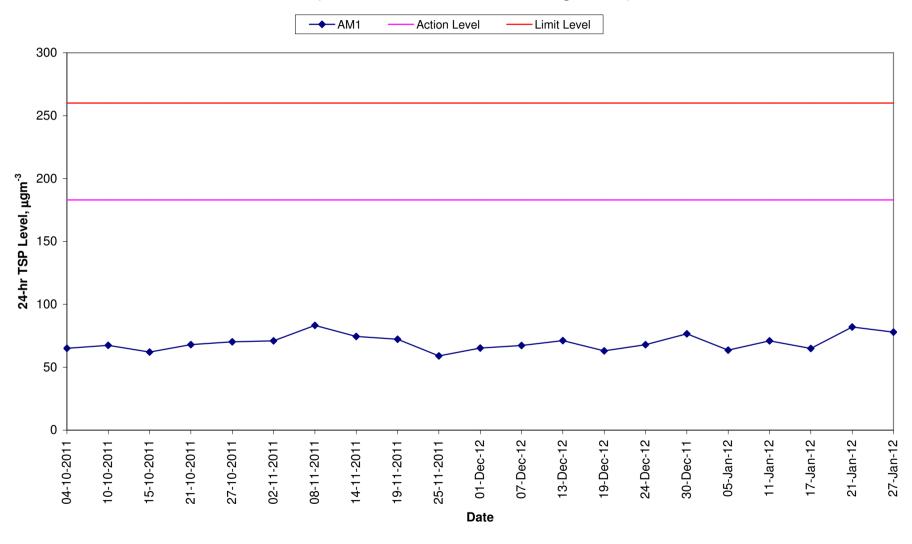

Annex G

Calibration Reports for HVSs

TSP Monitoring Equipment

Monitoring	Location	Monitoring Equipment		Last Calibration Dat	e Next Calibration Date
Station ID					
24-hr and 1-hr TSI	p	HVS	Calibrator		
AM1	Tuen Mun EMSD Vehicle Servicing Station	GMW GS-2310 (S/N 7580)	CM-AIR-43 (S/N 1785)	04 November 2011	04 January 2012
AM1	Tuen Mun EMSD Vehicle Servicing Station	GMW GS-2310 (S/N 7580)	CM-AIR-43 (S/N 1785)	04 January 2012	04 March 2012
AM2	River Trade Terminal Office	GMW GS-2310 (S/N 1252)	CM-AIR-43 (S/N 1785)	04 November 2011	04 January 2012
AM2	River Trade Terminal Office	GMW GS-2310 (S/N 1252)	CM-AIR-43 (S/N 1785)	04 January 2012	04 March 2012

<u>High-Volume TSP Sampler</u> 5-Point Calibration Record

Location : EMSD
Calibrated by : P.F.Yeung
Date : 04/01/2012

Sampler

Model : GMWS-2310 ACCU-VOL

Serial Number : S/N 7580

Calibration Orfice and Standard Calibration Relationship

Serial Number : 1785

 Service Date
 : 25 May 2011

 Slope (m)
 : 2.00506

 Intercept (b)
 : -0.02062

 Correlation Coefficient(r)
 : 0.99999

Standard Condition

Pstd (hpa) : 1013 Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1022 Ta(K) : 289

Resi	stance Plate	dH [green liquid]	Z	X=Qstd	IC	Y
		(inch water)		(cubic meter/min)		
1	18 holes	11.4	3.444	1.728	54	55.1
2	13 holes	9.6	3.160	1.586	48	49.0
3	10 holes	7.4	2.775	1.394	41	41.8
4	7 holes	4.6	2.188	1.101	30	30.6
5	5 holes	2.7	1.676	0.846	20	20.4

Sampler Calibration Relationship

 $Slope(m): \underline{38.967} \quad Intercept(b): \underline{-12.500} \qquad \qquad Correlation \ Coefficient(r): \underline{0.9998}$

Checked by: Magnum Fan Date: 10/01/2012

<u>High-Volume TSP Sampler</u> <u>5-Point Calibration Record</u>

Location:River TradeCalibrated by:P.F.YeungDate:04/01/2012

Sampler

Model : GMWS-2310 ACCU-VOL

Serial Number : S/N 1252

Calibration Orfice and Standard Calibration Relationship

Serial Number : 1785

 Service Date
 : 25 May 2011

 Slope (m)
 : 2.00506

 Intercept (b)
 : -0.02062

 Correlation Coefficient(r)
 : 0.99999

Standard Condition

Pstd (hpa) : 1013 Tstd (K) : 298.18

Calibration Condition

Pa (hpa) : 1022 Ta(K) : 289

Resi	Resistance Plate dH [green liquid]		Z	X=Qstd	IC	Y
	(inch water			(cubic meter/min)		
1	18 holes	11.0	3.383	1.697	64	65.3
2	13 holes	9.0	3.060	1.536	57	58.1
3	10 holes	7.0	2.699	1.356	49	50.0
4	7 holes	4.3	2.115	1.065	36	36.7
5	5 holes	2.7	1.676	0.846	26	26.5

Sampler Calibration Relationship

Slope(m):45.541 Intercept(b): -11.888 Correlation Coefficient(r): 0.9999

Checked by: Magnum Fan Date: 10/01/2012

Annex H

Event/Action Plan for Air Quality Monitoring

Table H1 Event Action Plan for Air Quality Monitoring

Action Level/Limit Level	Environmental Team Leader (ETL)	Independent Environmental Checker (IEC)	Supervising Officer Representative (SOR)	Contractor
Action Level				
Exceedance for one sample	 Identify source, investigate the causes of complaint and propose remedial measures; Inform IEC and SOR; Repeat measurement to confirm findings; Increase monitoring frequency to daily. 	 Check monitoring data submitted by ET; Check Contractor's working method. 	Notify Contractor and DSD.	 Rectify any unacceptable practice; Amend working methods if appropriate.
Exceedance for two or more consecutive samples	 Identify source; Inform IEC and SOR; Advise the SOR on the effectiveness of the proposed remedial measures; Repeat measurements to confirm findings; Increase monitoring frequency to daily; Discuss with IEC and Contractor on remedial actions required; If exceedance continues, arrange meeting with IEC and SOR; If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ET on the effectiveness of the proposed remedial measures; Supervise Implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor and DSD; Ensure remedial measures properly implemented. 	 Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate.

Action Level/Limit Level	Environmental Team Leader (ETL)	Independent Environmental Checker (IEC)	Supervising Officer Representative (SOR)	Contractor
Limit Level				
Exceedance for one sample	 Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC, SOR, DSD and EPD; Repeat measurement to confirm finding; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD, DSD and SOR informed of the results. 	on possible remedial measures;	 Confirm receipt of notification of exceedance in writing; Notify Contractor; Ensure remedial measures properly implemented. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; Amend proposal if appropriate.
Exceedance for two or more consecutive samples	 Notify IEC, SOR, DSD and EPD; Identify source; Repeat measurement to confirm findings; Increase monitoring frequency to daily; Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; Arrange meeting with IEC and SOR to discuss the remedial actions to be taken; Assess effectiveness of Contractor's remedial actions and keep IEC, EPD, DSD and SOR informed of the results; If exceedance stops, cease additional monitoring. 	 Discuss amongst SOR, ET, and Contractor on the potential remedial actions; Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the SOR accordingly; Supervise the implementation of remedial measures. 	 Confirm receipt of notification of exceedance in writing; Notify Contractor; In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IEC within three working days of notification; Implement the agreed proposals; Resubmit proposals if problem still not under control; Stop the relevant portion of works as determined by the SOR until the exceedance is abated.

Annex I

Implementation Schedule of Mitigation Measures

Annex I Summary of Mitigation Measures Implementation Schedule

Type of Impact	Environmental Protection Measures	Location/ Timing	Status				
Summary of Envi	Summary of Environmental Mitigation Measures in the EIA and EM&A Manual						
Construction Pha	Construction Phase						
Air Quality	Dust mitigation measures stipulated in <i>the Air Pollution Control</i> (<i>Construction Dust</i>) <i>Regulation</i> shall be incorporated to control Post emission. Notice shall be given to authority prior to commencing of work.	Work sites / during construction period	Δ. Notice of works commencement was submitted to EPD on 3 August 2010.				
Water Quality	The practices outlined in ProPECC PN 1/94 Construction Site Drainage should be adopted. It is recommended to install perimeter channels in the works areas to intercept runoff as site boundary prior to the commencement of any earthwork. To prevent storm runoff from washing across exposed soil surfaces, intercepting channels should be provided. Drainage channels are also required to convey site runoff to sand/silt traps and oil interceptors. Provision of regular cleaning and maintenance can ensure the normal operation of these facilities throughout the construction period. Any practical options for the diversion and re-alignment of drainage should comply with both engineering and environmental requirements in order to ensure adequate hydraulic capacity of all drains.	Work site/During the construction period	Δ				
Water Quality	There is a need to apply to EPD for a discharge license under the WPCO for discharging effluent from the construction site. The discharge quality is required to meet the requirements specified in the discharge license. All the runoff and wastewater generated from the works areas should be treated so that it satisfies all the standards listed in the TM-DSS. Reuse and recycling of the treated effluent can minimize water consumption and reduce the effluent discharge volume. The beneficial uses of the treated effluent may include dust suppression, wheel washing and general cleaning. If monitoring of the treated effluent quality from the works areas is required during the construction phase of the Project, the monitoring should be carried out in accordance with the WPCO license which is under the ambit of regional office (RO) of EPD.	Work site/During the construction period	Δ. Discharge licence was awarded by EPD on 7 December 2010.				
Water Quality	The construction programme should be properly planned to minimize soil excavation, if any, in rainy seasons. This prevents soil erosion from	Work site/During the construction period	Δ				

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Impuct	exposed soil surfaces. Any exposed soil surfaces should also be properly protected to minimize dust emission. In areas where a large amount of exposed soil exists, earth bunds or sand bags should be provided. Exposed stockpiles should be covered with tarpaulin or impervious sheets at all times. The stockpiles of materials should be placed at locations away from any stream course so as to avoid releasing materials into the water bodies. Final surfaces of earthworks should be compacted and protected by permanent work. It is suggested that haul roads should be paved with concrete and the temporary access roads protected using crashed stone or gravel, wherever practicable. Wheel washing facilities should be provided at all site exists to ensure that earth, mud and debris would not be carried out of the works areas by vehicles.		
Water Quality	Good sites practices should be adopted to clean the rubbish and litter on the construction sites so as to prevent the rubbish and litter from spreading from the site area. It is recommended to clean the construction sites on a regular basis.	Work site/During the construction period	Δ
Water Quality	The presence of construction workers generates sewage. It is recommended to provide sufficient chemical toilets in the works areas. The toilet facilities should be more than 30m from any watercourse. A licensed water collector should be deployed to clean the chemical toilets on a regular basis. The construction workers can also make use of the existing toilet facilities within the PPSTW as necessary.	Work site/During the construction period	√
Water Quality	Notices should be posted at conspicuous locations to remind the workers not to discharge any sewage or wastewater into the nearby environment during the construction phase of the project. Regular environmental audit on the construction phase of the project. Regular environmental audit on the construction site can provide an effective control of any malpractices and can achieve continual improvement of environmental performance on site.	Work site/During the construction period	√
Waste Management	Contractor must register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in	Work site/During the construction period	√

Type of	Environmental Protection Measures	Location/ Timing	Status
Impact	particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.		
Waste Management	Any service shop and maintenance facilities should be located on hard standings within a bunded area, and stumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should only be undertaken within the areas appropriately equipped to control these discharges.	Work site/During the construction period	<>
Waste Management	Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with the chemical wastes. General requirements are given as follows: • Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport. • Chemical waste containers should be suitably labelled, to notify and warn the personnel who are handling the wastes, to avoid accidents. • Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.	Work site/During the construction period	
Waste Management	 Good Site Practices Recommendations for good site practices during the construction activities include: Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site Training of site personnel in proper waste management and chemical handling procedures Provision of sufficient waste disposal points and regular collection of waste Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by 	Work site/During the construction period	

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
•	 transporting wastes in enclosed containers Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility. 		
Waste Management	 Waste Reduction Measures Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include: Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal. Encourage collection of aluminium cans by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force Proper storage and site practices to minimise the potential for damage or contamination of construction materials. Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 	Work site/During planning & design stage, and construction stage	
Waste Management	General Refuse General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector should be employed by the contractor to remove general refuse from the site, separately from C&D material. Preferably an enclosed and covered area should be provided to reduce the occurrence of 'wind blown' light material.	Work site / During the construction period	
Waste Management	Construction and Demolition Material In order to minimise the impact resulting from collection and	Work site / During design stage & construction period	√

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	transportation of C&D material for off-site disposal, the excavated material generated from site formation works for the proposed new facilities and units at the STW should be reused on-site as far as practicable. The surplus excavated material should be disposed of at the designated public fill reception facility, as agreed with the Secretary of the Public Fill Committee, for other beneficial uses.		
Waste Management	 Mitigation measures and good site practices should be followed to control potential environmental impact from handling and transportation of C&D material. The mitigation measures include: Where it is unavoidable to have transient stockpiles of C&D material pending collection for disposal, the transient stockpiles shall be located away from waterfront or storm drains as far as possible. Open stockpiles of construction materials or construction wastes onsite should be covered with tarpaulin or similar fabric. Skip hoist for material transport should be totally enclosed by impervious sheeting. Every vehicle should be washed to remove any dusty materials from its body and wheels before leaving a construction site The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores. The load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle. All dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet. The height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading. 	Work site / During design stage & construction period	♦
Waste Management	When disposing C&D material at a public filling facility, it shall be noted that the material shall only consist of earth, building debris and broken rock and concrete. The material shall be free from marine mud,	Work site/During design stage & construction period	√

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered to be unsuitable by the Filling Supervisor. In order to monitor the disposal of the surplus C&D material at the designed public fill reception facility and to control fly tipping, a trip-ticket system should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work with reference to the ETWB TCW No. 31/2004 "Trip Ticket System for Disposal of Construction and Demolition Materials" as attached in Appendix 7-1. An Independent Environmental Checker should be responsible for auditing the results of the system.		
Waste Management	If chemical wastes are produced at the construction site, the Contractor would be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes, to either the Chemical Waste Treatment Centre, or another licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	
Landscape & Visual	Temporary Tree Nurseries Temporary tree nurseries may be set up for the transplanted tree and proposed trees at an early stage to allow small trees to grow during the construction periods. By the time when planting area becomes available, trees mature and increase in trunk & spread size. They will require minimal pruning and suffer much less damage during transplanting when comparing the travel distance from an on-site nursery to an off-site nursery.	Work site/During design stage & construction period	$\sqrt{.}$ A tree nursery has been set up off-site near the site office.

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
	Besides, these trees may also be positioned as visual mitigation during the construction period.		
Landscape & Visual	No-intrusion Zone To maximize protection to existing trees and ground vegetation, construction contracts may designate "No-intrusion Zone" to various areas within the site boundary with rigid and durable fencing for each individual no-intrusion zone. The contractor should close monitor and restrict the site working staff not to enter the "no-intrusion zone", even for non-direct construction activities and storage of equipment.	Work site/During design stage & construction period	<>
Landscape & Visual	Hoarding Hoarding or boundary fencing for construction shall be considered. It should be sensitively designed, subtle, camouflaged and more 'permeable' so that they fit into the existing environment when looking from outside.	Work site/During design stage & construction period	√
Landscape & Visual	Dust and Erosion Control for Exposed Soil Excavation works and demolition of existing building blocks and which will be highly visible form surrounding areas should be well planned and with precautions to suppress dust. Exposed soil shall be covered or 'camouflaged' and watered often. Areas that are expected to be left with bare soil for a long period of time after excavation shall be properly covered with suitable protective fabric. Silt and erosion shall be controlled by ground barriers around the slope cutting area	Work site/During design stage & construction period	
Landscape & Visual	Existing Tree Record Inventory All retained trees should be record photographically at the commencement of the Contract, and carefully protected during the construction period. Detailed tree protection specification shall be allowed and included in the Contract Specification, which specifying the	Work site/During design stage & construction period	<>>

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Impact	tree protection requirement, submission and approval system, and the tree monitoring system.		
Landscape & Visual	Construction Light All security floodlights for construction sites shall be equipped with adjustable shield, frosted diffusers and reflective covers, and be carefully controlled to minimize light pollution and night-time glare to nearby residences and GIC users. The Contractor shall consider other security measures which shall minimize the visual impacts.	Work site / During design stage & construction period	√ ·
Landscape & Visual	Tree Transplanting Apart from the 18 numbers of "Leucaena leucocephala", which are proposed to be felled in accordance with ETWB TCW No. 3/2006, all the affected trees shall be transplanted. Where practicable, trees shall be directly transplanted to permanent on-site locations. The location of the transplanted tree is shown in Figure 8.9.1.	Work site / During design stage & construction period	Δ . Tree transplantation in progress.
Landscape & Visual	Tree Compensation Ratio The total number of compensatory trees planted in the project area shall not be less than 1:1 ratios by new trees. Required numbers and locations of compensatory trees shall be determined and agreed with Government during the tree felling application process under ETWCTC 3/2006. Compensatory trees shall be at least heavy standard size to create "immediate" greening effect. 81 numbers of "Cassia surattensis" will be provided as the additional compensatory planting for loss of greenery in the area due to removal of the affected trees. The location of the additional compensatory planting is shown in Figure 8.9.1.	Work site / During design stage & construction period	N/A
Landscape & Visual	Re-use of Existing Soil and Advance formation of Planting Area Existing topsoil shall be re-used where possible for new planting areas within the project. Advance formation of planting area and early implementation of the plating works can minimize adverse impact on trees. The construction program shall consider using the soil removed	Work site / During design stage & construction period	√ ·

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
- Impact	from one phase for backfilling another. Suitable storage ground, gathering ground and mixing ground may be set up on-site as necessary.		
Landscape & Visual	Establishment Period 12 month establishment period for the soft landscape works will be allowed in the main contract. Most construction contracts in Hong Kong require the Contractor to carry out routine horticultural operations, including watering, pruning, weeding, pest control, replacement of dead plants etc. to ensure healthy establishment of new planting during a 12 month establishment period. This period also serves as a kind of warranty / guarantee on the quality of the plants supplied and installed by the Contractor. Monthly monitoring during the first year of establishment period is recommended.	Work site/During operation period	N/A. To be implemented during operation phase of Project.
Landscape & Visual	Re-instatement of excavated Area All excavated area and disturbed area for utilities diversion, temporary road diversion, and pipeline woks will be reinstated to former conditions, subject to applicable Government Standards.	Work site / During design stage & operation period	N/A. To be implemented during operation phase of Project.
Landscape & Visual	Appearance and Greening for the proposed structures Compatible design, construction materials and surface finishes of the proposed structure should match with the nearby existing external appearance of PPSTW buildings for achieving visual uniformity. Finishing materials shall have due consideration to form, basic color, color/tone variation, micro-and macro-texture, and reflectivity/light absorbance to avoid glare. Planting, such as turf, low groundcovers and climbers, may also be planted on top of these elements to provide greening and aesthetic effect.	Work site / During design stage & operation period	N/A. To be implemented during operation phase of Project.
Summary of Key	Environmental Mitigation Measures in Contract Requirements	1	
Air Quality	Only Ultra-low-sulphur diesel (ULSD) should be used for all diesel- operated plants and equipments on site	Work sites / during construction period	V
Air Quality and Noise	Plants and equipments of good operation conditions should be used on site.	Work sites / during construction period	V
Noise	No diesel hammers should be used for piling works	Work sites / during construction period	√

Type of Impact	Environmental Protection Measures	Location/ Timing	Status
Noise	Construction Noise Permits (CNP) should be applied for works conducted outside non-restricted hours.	Work sites / during construction period	V
Noise	Quiet construction equipments and the quietest practicable working methodologies should be adopted for works whenever feasible. Noise labels should be provided for air compressors. Hoods and cover panels of generators and air compressors should be closed during operation. Noise labels should be provided for air compressors and hand-held percussive breakers.	Work sites / during construction period	√
Waste Management	Temporary works construction on site should minimize the use of timber to reduce the quantity of C&D waste generated during works period.	Work sites / during construction period	√
Landscape and Visual	Retained or to-be-transplanted trees on site should be properly protected from physical damages and soil compacts with temporary fencing or hessian armouring whenever feasible.	Work sites / during construction period	<>

Remark:

- √ Compliance of Mitigation Measures
- Compliance of Mitigation but need improvement
- x Non-compliance of Mitigation Measures
- Non-compliance of Mitigation Measures but rectified by ATAL-Degrémont-China State JV
- Δ Deficiency of Mitigation Measures but rectified by ATAL-Degrémont-China State JV
- N/A Not Applicable in Reporting Period

Annex J

Waste Flow Table

Contract No.: DC/2008/03 - Design, Build and Operate Pillar Point Sewage Treatment Works

Monthly Summary Waste Flow Table

	Ac	tual Quantities of Inc	ert C&D Materials	(Public Fill) Generat	ed	Actu	al Quantities of Non-i	nert C&D Materials	(Construction Waste	e) Generated
Month	Total Quantity Generated	Rocks & Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Metals (see Note 1)	Paper/ cardboard packaging (see Note 1)	Plastics (see Note 2)	Chemical Waste	Others, e.g. general refuse (see Note 3)
	tonne	tonne	tonne	tonne	tonne	kilogram	kilogram	kilogram	Litre	tonne
Nov 2010	2,248	0	0	0	2,248	60	100	0	0	18.05 (see Note 4)
Dec 2010	11,314 (see Note 4)	0	0	0	11,314	100	120	20	0	28.4 (see Note 4)
Jan 2011	58,383 (see Note 4)	0	0	0	58,383	250	280	60	0	4.59 (see Note 4)
Sub-total	71,945	0	0	0	71,945	410	500	80	0	51.04
Feb 2011	12,855	0	0	0	12,855	100	150	50	0	2.43 (see Note 4)
Mar 2011	22,859	0	0	0	22,859	150	180	55	0	9.02
Apr 2011	8,547 (see Note 7)	0	0	5,684(see Note 5, 7)	2,863 (see Note 7)	50	30	15	0	5.78
Sub-total	44,261	0	0	5,684	38,577	300	360	120	0	17.23
May 2011	6,293 (see Note 7)	0	0	11 (see Note 5, 7)	6,282 (see Note 7)	45	25	10	360 (see Note 7)	8.83
Jun 2011	4,587 (see Note 7)	0	0	0 (see Note 7)	4,587 (see Note 7)	40	30	15	0	7.10
Jul 2011	523	0	0	0	523	15	5	10	0	7.20
Sub-total	11,403	0	0	11	11,392	100	60	35	360	23.13
Aug 2011	571 (see Note 11)	0	0	0	571 (see Note 11)	0	0	15	450 (see Note 8)	6.12
Sept 2011	235	0	0	0	235	20	0	0	0	12.15 (see Note 9)
Oct 2011	5,705 (see Note 10)	0	0	0	5,705 (see Note 10)	100	0	0	0	2.98
Sub-total	6,511	0	0	0	6,511	120	0	15	450	21.25
Nov 2011	6,294	0	0	0	6,294	50	0	0	0	44.84
Dec 2011	3,011	0	0	0	3,011	20	0	0	0	17.14
Jan 2012	285	0	0	0	285	20	0	0	0	49.01
Sub-total	9,590	0	0	0	9,590	90	0	0	0	110.99
Total	153,015	0	0	5,695	147,320	1,090	920	250	810	285.62

Notes:

- (1) Metal and paper/cardboard packaging were collected by recycler for recycling.
- (2) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material collected by recycler for recycling.
- (3) General refuse was disposed of at WENT by subcontractors.
- (4) The waste flow data for November and December 2010, January and February 2011 was updated in March 2011based on SOR's comments and has been confirmed by the Contractor.
- (5) The inert C&D materials were reused in the Contract No. EP/SP/58/08 at Tuen Mun Tsang Tsui.
- (6) Chemical waste was collected though the licensed chemical waste collector, Dunwell Ind. (Holdings) Ltd, with the waste collection licence number 7111-757-W0015-WC.
- (7) The waste flow data for April, May and June 2011 was updated in August 2011 based on SOR's comments and has been confirmed by the Contractor.
- (8) The waste flow data of chemical waste for August 2011 was updated in October 2011 based on Contractor's revised waste flow summary.
- (9) The waste flow data of general refuse for September 2011 was updated in November 2011 based on Contractor's revised waste flow summary.
- (10) The waste flow data of C&D material for October 2011 was updated in December 2011 based on Contractor's revised waste flow summary.
- (11) The waste flow data of C&D material for August 2011 was updated in January 2011 based on SOR's comments and has been confirmed by the Contractor.

Annex K


Environmental Complaint, Environmental Summon and Presecution Log

Annex K Cumulative Complaint and Summons/Prosecutions Log

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
November 2010	0	0
December 2010	0	0
January 2011	0	0
February 2011	0	0
March 2011	0	0
April 2011	0	0
May 2011	0	0
June 2011	0	0
July 2011	0	0
August 2011	0	0
September 2011	0	0
October 2011	0	0
November 2011	0	0
December 2011	0	0
January 2012	0	0
Overall Total	0	0

Annex L

Construction Programme of the Project

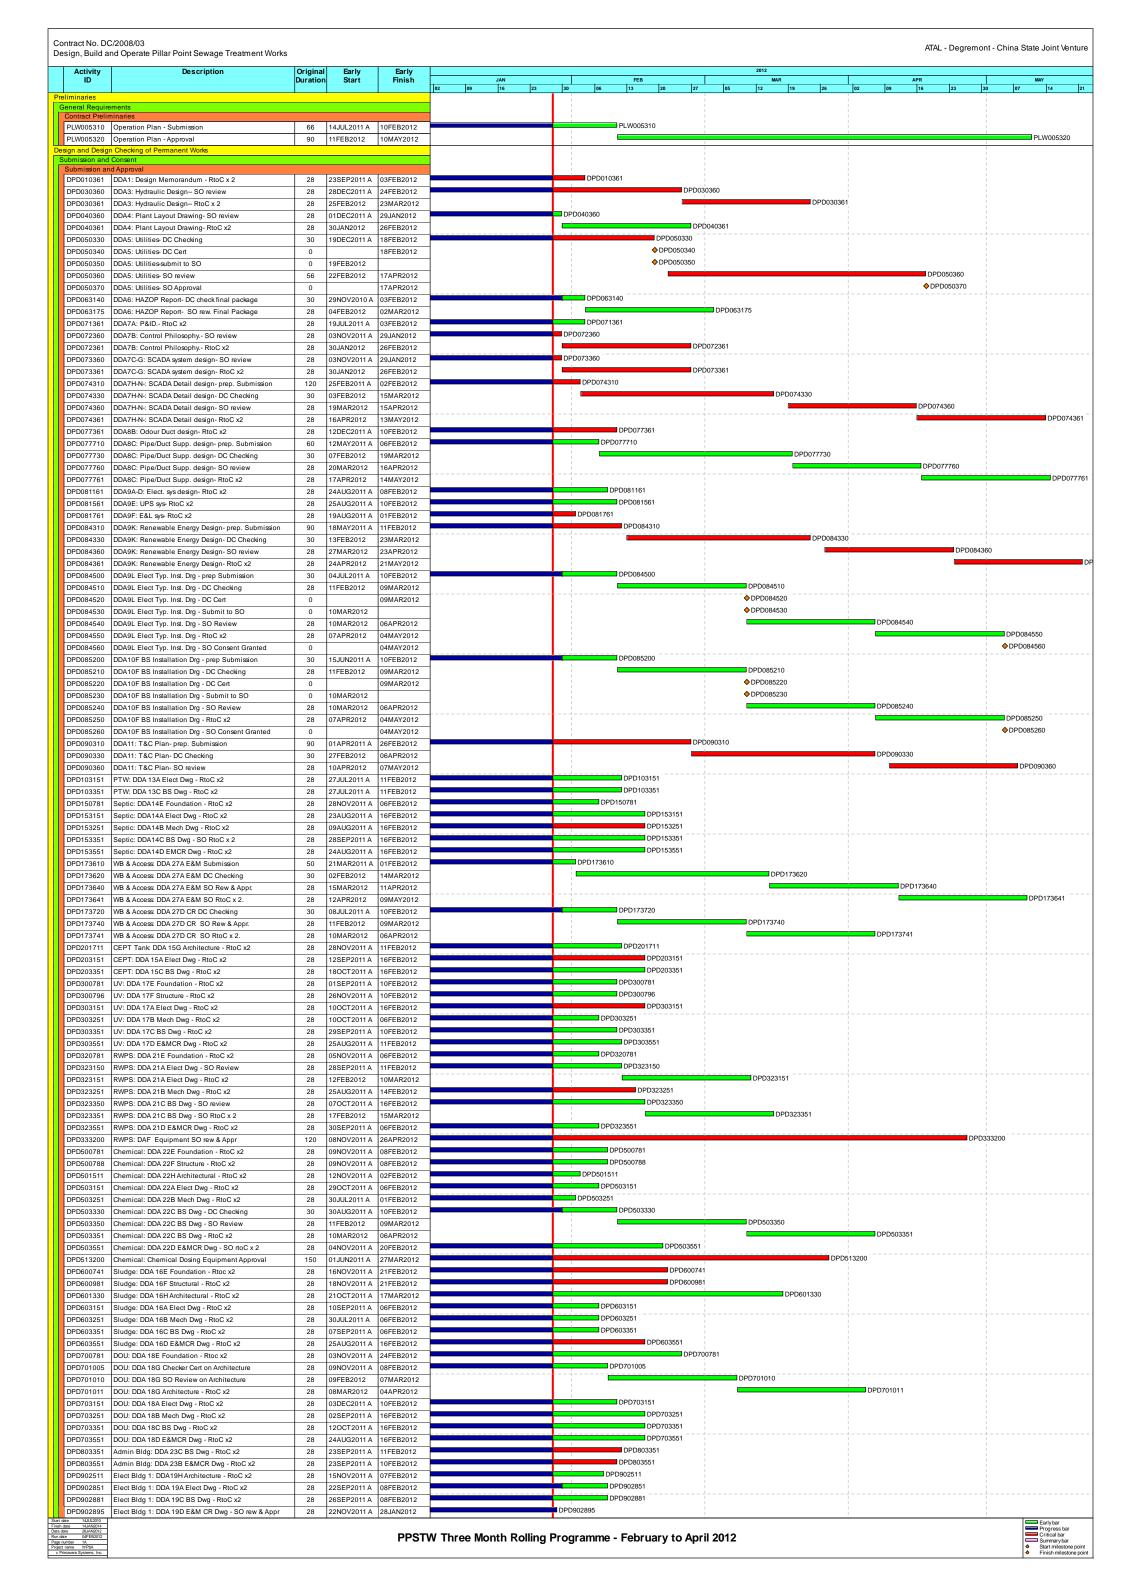

Contract No. DC/2008/03 ATAL - Degremont - China State Joint Venture Design, Build and Operate Pillar Point Sewage Treatment Works CCC200420 CEPT Tank Beam and Slab Bay 2 Zone 1 45 27FEB2012 11APR2012 CCC200430 CCC200430 | CEPT Tank Beam and Slab Bay 2 Zone 2 45 23MAR2012 06MAY2012 CCC200440 | CEPT Tank Beam and Slab Bay 4 Zone 3 42 25APR2012 05JUN2012 14APR2012 25MAY2012 CCC200450 | CEPT Tank Beam and Slab Bay 4 Zone 4 42 CCC200460 CCC200460 | CEPT Tank Beam and Slab Bay 5 45 | 18MAR2012 | 01MAY2012 CCC200470 | CEPT: Roof Slab East Part 75 16APR2012 29JUN2012 CCC200480 | CEPT: Mass Concrete Bay 2 Zone 1 30 30APR2012 29MAY2012 CCC200630 | CEPT: Backfill at NW for UV and SDB 36 08FEB2012 | 14MAR2012 28MAR2012 02MAY2012 CCC200640 CCC200640 | CEPT: Backfill for MCC Room 36 CCC200650 | CEPT: Remaining Backfill 45 03MAY2012 | 16JUN2012 CCC920110 CCC920110 | CEPT MCC Rm: Formation and Blinding 2 03MAY2012 04MAY2012 CCC920120 | CEPT MCC Rm: Fdn-Cable Trench &On-Grade Slab 18 05MAY2012 26MAY2012 66 16FEB2012 21APR2012 CCC110165 PTWN: Wall Stem Grid 1 to 4 up +2 to +5.45 CCC111510 PTWN: Wall & Top Roof +2 to +5.45 Grid 4 to 6 50 28FEB2012 17APR2012 CCC112165 PTWN: Water Tightness Test 28JAN2012 25FEB2012 07APR2012 CCC112170 PTWN: Backfilling 42 26FEB2012 CCC112175 PTWN: Remaining Backfill 23APR2012 16MAY2012 20 CCC112180 PTWN: ABWF Work 70 01APR2012 09JUN2012 17JAN2012 A 16FEB2012 CCC112218 PTWS: Grit Chamber Base 21 CCC112245 PTWS: Grit Chamber Cone 17FEB2012 10APR2012 54 CCC112320 PTWS: Raft Footing for Channel 11APR2012 17APR2012 CCC113110 PTWS: Grit Chamber (Upper Chamber Wall) 1 & 2 13MAR2012 01APR2012 20 CCC113120 PTWS: Grit Chamber (Upper Chamber Wall) 3 & 4 02APR2012 21APR2012 CCC113150 PTWS: Water Test to Grit Chamber 22APR2012 21MAY2012 30 CCC114100 CCC114100 PTWS: Formation of Fine Screen Chamber 10 31MAR2012 09APR2012 CCC114110 PTWS: Fine Screen Chamber 50 10APR2012 29MAY2012 CCC140300 PTWS: Flowmeter Chamber & Pipe works 15APR2012 28JUN2012 CCC150010 PTW: MCC Room 08APR2012 21JUN2012 75 CCC150020 PTW: Formation to MCC Room 08APR2012 10APR2012 CCC150030 PTW: Raft Footing to MCC Room 10 11APR2012 20APR2012 CCC150040 PTW: Cable Trench & Floor Slab to MCC Room 18 21APR2012 08MAY2012 CCC300130 UV: Excavation 24 15FEB2012 13MAR2012 14MAR2012 06APR2012 CCC300131 UV: Outlet Pit CCC300132 CCC300132 UV: Vertical Blinding 07APR2012 14APR2012 CCC300136 UV: Backfill and Formation to Channel 17APR2012 27APR2012 CCC300136 10 28APR2012 22MAY2012 CCC300138 UV: Inlet & Outlet Channel 20 CCC300140 UV: Raft Foundation 900mm thk 20 28APR2012 22MAY2012 CCC600230 CCC600230 SDB: Southern Raft Foundation - 1500mm thk 14 02JAN2012 A 31JAN2012 CCC600250 CCC600250 SDB: Southern Holding Tanks (Bottom Pour) 18 01FEB2012 21FEB2012 CCCennsen 22FEB2012 27FEB2012 CCC600270 CCC600270 | SDB: Install Temporary Strut at +4.0 28FEB2012 05MAR2012 CCC600280 06MAR2012 16MAR2012 CCC600290 15 17MAR2012 03APR2012 CCC600300 SDB: Norhtern Holding Tanks (Bottom Pour) CCC600300 05APR2012 24APR2012 25APR2012 04MAY2012 CCC600310 CCC600320 SDB: Remove Strut at +4.0 CCC600320 05MAY2012 11MAY2012 CCC600370 CCC150110 Septic: Temp Earth Lateral Support 12 17APR2012 30APR2012 CCC150110 02MAY2012 10MAY2012 CCC150120 CCC150120 Septic: Excavation CCC500110 CCC500110 Chemical Bldg: Excavation 12 11APR2012 27APR2012 CCC500120 CCC500120 Chemical Bldg: Raft Fdn - 750 thk, On-Grade Slab 14 28APR2012 15MAY2012 CCC800140 CCC800140 Admin Bldg: Underground Drainage Work 28JAN2012 06FEB2012 CCC800160 CCC800160 Admin Bldg: Beams & Slab at G/F 12 09FEB2012 20FEB2012 CCC800200 CCC800200 Admin Bldg: Water Tank - Roof Slab & Beams 21FEB2012 01MAR2012 CCC800220 CCC800220 Admin Bldg: Walls & Columns - G/F to 1/F 15 21FEB2012 06MAR2012 CCC800230 CCC800230 Admin Bldg: Beams & Slab at 1/F 07MAR2012 17MAR2012 CCC800240 CCC800240 Admin Bldg: Walls & Columns - 1/F to R/F 14 18MAR2012 31MAR2012 CCC800250 Admin Bldg: Beams & Slab at R/F 12 01APR2012 | 12APR2012 CCC800250 CCC800260 CCC800260 Admin Bldg: Walls & Columns - R/F to TRF 10 13APR2012 22APR2012 CCC800270 CCC800270 Admin Bldg: Beams & Slab at TR/F 10 23APR2012 02MAY2012 CCC800280 Admin Bldg: ABWF Works 60 10APR2012 08JUN2012 CCC910110 | Elect Bldg 1: Excavation 12 28DEC2011 A | 03FEB2012 CCC910115 CCC910115 | Elect Bldg 1: Demolish Part of Extg Tx Room 6 04FEB2012 10FEB2012 CCC910120 CCC910120 Elect Bldg 1: Fdn-Cable Trench &On-Grade Slab 20 11FEB2012 05MAR2012 CCC910130 CCC910130 | Elect Bldg 1: Walls - G/F to R/F 24 06MAR2012 02APR2012 CCC910140 | Elect Bldg 1: Roof Slab 18 03APR2012 27APR2012 CCC910145 CCC910145 | Elect Bldg 1: Demolish Brickwall of Extg Tx Room 12 28APR2012 12MAY2012 CCC910150 Elect Bldg 1: Remove Temp Support 18 28APR2012 19MAY2012 CCC930110 CCC930110 Elect Bldg 3: Excavation 6 20FEB2012 25FEB2012 CCC930120 CCC930120 | Elect Bldg 3: Fdn-Cable Trench &On-Grade Slab 27FEB2012 | 17MAR2012 CCC930130 CCC930130 | Elect Bldg 3: Walls - G/F to R/F 12 19MAR2012 31MAR2012 CCC930140 CCC930140 | Elect Bldg 3: Roof Slab 24 | 02APR2012 | 04MAY2012 CCC930150 Elect Bldg 3: Remove Formwork 18 05MAY2012 26MAY2012 380 12APR2012 27JUL2013 CCM101800 Installation of Sitewide Drainage 05APR2012 20JUL2013 CCM102000 Installation of Sitewide Sewerage CCM102020 Pipe Line bet N2 to PTW and Manholes N2 & N3 150 31MAR2012 03OCT2012 22APR2012 17MAR2013 CCM102100 Laying Pipe Ducts, Trenches and Utilities ■EMW110110 EMW110110 | Coarse Screen: Equipment Manufacturing and Test 180 21NOV2011 A 28APR2012 EMW110120 Coarse Screen: Delivery of E&M Equipment On Site 45 29APR2012 12JUN2012 EMW140410 EMW140410 Grit: E&M Equipment Procurement 180 21NOV2011 A 25APR2012 EMW140420 Grit: Delivery of E&M Equipment On Site 42 26APR2012 06JUN2012 EMW152100 | Septic Station: Delivery of E&M Equipment 180 07MAY2012 02NOV2012 ■EMW200100 150 21NOV2011 A 07MAY2012 EMW200100 | CEPT: E&M Equipment Procurement EMW301100 UV: E&M Equipment Procurement 180 | 17FEB2012 | 14AUG2012 210 27APR2012 22NOV2012 EMW322200 RWPS: E&M Equipment Procurement EMW501000 | Chemical: E&M Equipment Procurement 150 28MAR2012 24AUG2012 240 28JAN2012 23SEP2012 EMW601000 Sludge: E&M Equipment Procurement 180 11FEB2012 08AUG2012 EMW711100 DOUA: E&M Equipment Procurement EMW721100 DOU B: E&M Equipment Procurement 180 21APR2012 17OCT2012 EMW802100 Admin Bldg : SCADA Eq. Procurement 80 27FEB2012 16MAY2012 EMW802150 60 28JAN2012 27MAR2012 EMW802150 Admin Bldg : ELV Eq. Procurement EMW802250 EMW802250 Admin Bldg : Delivery of ELV Eq. On site 30 28MAR2012 26APR2012 EMW802350 Admin Bldg : ELV Equipment Installation 90 27APR2012 14AUG2012 EMW811100 SHB Bldg: E&M Equipment Procurement 60 15MAR2012 | 13MAY2012 220 17FEB2012 10NOV2012 EMW821010 Flowmeter: E&M Equipment Procurement EMW942100 CB Main SW Rm: Mat'l & Equipment Procurement 160 09FEB2012 17JUL2012 EMW943100 Elect Bldg 3: Mat'l & Equipment Procurement 160 05FEB2012 13JUL2012
