
REPORT



Installation of Submarine Gas Pipelines and Associated Facilities from To Kwa Wan to North Point for Former Kai Tak Airport Development

Eighth Quarterly Environmental Monitoring & Audit (EM&A) Report

3 July 2014

Environmental Resources Management 16/F Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone 2271 3000 Facsimile 2723 5660



www.erm.com



Environmental Resources

Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660

E-mail: post.hk@erm.com http://www.erm.com

16/F Berkshire House

25 Westlands Road Quarry Bay, Hong Kong

Management

Installation of Submarine Gas Pipelines and Associated Facilities from To Kwa Wan to North Point for Former Kai Tak Airport Development

Eighth Quarterly Environmental Monitoring & Audit (EM&A) Report

Document Code: 0158059_8th Quarterly EM&A_v0.doc

Client:		Project N	0:		
MKJV		015805	9		
Summary		Date:			
		3 July 2			
		Approved	by:		
Monitorin Submarir	ument presents the Eighth Quarterly Environmental g and Audit (EM&A) Report for the Installation of ne Gas Pipelines and Associated Facilities from To Kwa lorth Point for Former Kai Tak Airport Development.	ling	2.1		
wanton	ionth Point for Former Kar rak Airport Development.	Mr Crai	a Reid		
		Partner	g noid		
v0	8 th Quarterly EM&A Report	RC	JT	CAR	3/7/14
Revision	Description	Ву	Checked	Approved	Date
name of 'EF terms of the Business ar	has been prepared by Environmental Resources Management the trading RM Hong-Kong, Limited', with all reasonable skill, care and diligence within the Contract with the client, incorporating our General Terms and Conditions of ad taking account of the resources devoted to it by agreement with the client.	Distributio	ernal		5 18001:2007 No. OHS 515956
We disclaim the scope of	any responsibility to the client and others in respect of any matters outside f the above.	🛛 Pul	olic		BSI
nature to thi	s confidential to the client and we accept no responsibility of whatsoever rd parties to whom this report, or any part thereof, is made known. Any such on the report at their own risk.	🗌 Coi	nfidential	ISO 5 Certificat	001 : 2008 e No. FS 32515





Installation of Submarine Gas Pipelines and Associated Facilities from To Kwa Wan to North Point for Former Kai Tak Airport Development

Environmental Certification Sheet Environmental Permit No. EP-401/2010

Reference Document/Plan

Document/Plan-to be Certified/ Verified:

Eighth Quarterly Environmental Monitoring & Audit (EM&A) Report – March to May 2014

Date of Report: 3/7/2014

Date prepared by ET: 3/7/2014

Date received by IEC: 3/7/2014

Reference EM&A Manual Requirement

EM&A Manual Requirement:

Section 12.4 iii

Content: Quarterly EM&A Summary Report

12.4 "The Quarterly EM&A Summary Report which should generally be around 5 pages (including about 3 of text and tables and 2 of figures) should contain at least the following information".

ET Certification

I hereby certify that the above referenced document/plan complies with the above referenced section of the EM&A Manual.

Ms Winnie Ko, Environmental Team Leader:

3/7/2014

Date:

IEC Verification

I hereby verify that the above referenced document/ plan complies with the a	bove ref	erenced section of the
EM&A Manual.		
Dr Anne Kerr, Independent Environmental Checker:	Date:	08/07/2014

	EXECUTIVE SUMMARY	Ι
1	INTRODUCTION	- 1 -
1.1	PURPOSE OF THE REPORT	-1-
1.2	STRUCTURE OF THE REPORT	-1-
2	PROJECT INFORMATION	- 3 -
2.1	Project Background	- 3 -
2.2	GENERAL SITE DESCRIPTION	- 3 -
2.3	PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE	- 3 -
2.4	CONSTRUCTION ACTIVITIES UNDERTAKEN DURING THE REPORTING PERI	OD -3-
2.5	STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS	- 4 -
3	EM&A REQUIREMENTS	- 7 -
3.1	Marine Water Quality Monitoring	- 7 -
3.2	AIR-BORNE NOISE MONITORING	- 11 -
4	IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES	N - 13 -
5	MONITORING RESULTS	- 14 -
5.1	SITE INSPECTIONS & AUDITS	- 14 -
5.2	MARINE WATER QUALITY MONITORING	- 18 -
5.3	AIR-BORNE NOISE MONITORING	- 19 -
5.4	WASTE MANAGEMENT EM&A	- 20 -
6	ENVIRONMENTAL NON-COMFORMANCE	- 21 -
6.1	SUMMARY OF ENVIRONMENTAL NON-COMPLIANCE	- 21 -
6.2	SUMMARY OF ENVIRONMENTAL COMPLAINT	- 21 -
6.3	SUMMARY OF ENVIRONMENTAL SUMMON AND SUCCESSFUL PROSECUTIO	N - 21 -
7	FUTURE KEY ISSUES	- 22 -
7.1	CONSTRUCTION ACTIVITIES FOR THE COMING QUARTER	- 22 -
7.2	SOLID AND LIQUID WASTE MANAGEMENT STATUS	- 22 -
8	CONCLUSIONS	- 23 -

EXECUTIVE SUMMARY

The construction works of the installation of submarine gas pipelines and associated facilities from To Kwa Wan to North Point for former Kai Tak Airport Development ("the Project") commenced on 13 June 2012. This is the 8th Quarterly Environmental Monitoring and Audit (EM&A) Report presenting the EM&A works carried out during the quarterly period from 1 March to 31 May 2014 in accordance with the *EM&A Manual* of the Project ⁽¹⁾.

During the reporting period, environmental site inspections/ audits were carried out weekly by the representatives of the Contractor and the Environmental Team (ET). Joint site inspections were conducted on 25 March, 29 April and 27 May 2014 by the Contractor, the ET, the Resident Engineer (RE) and the Independent Environmental Checker (IEC). Environmental monitoring activities on marine water quality and air-borne noise have been undertaken in accordance with the requirements of the EM&A programme. Exceedances of Action and Limit Levels for water quality were recorded in thirty-nine (39) monitoring events. Following the review of monitoring data and marine works details in accordance with the procedures stipulated in the Event and Action Plan of EM&A Manual, these exceedances were considered to be due to natural variation in water quality characteristic of Hong Kong waters and were unlikely to be due to the Project's marine works activities. Environmental performance of the Project complied with the environmental requirements and all necessary mitigation measures were properly implemented.

No non-compliance with EIA recommendations, EP conditions and other requirements associated with the construction of the Project were recorded in this reporting period. No environmental complaint or environmental summons was received in this quarterly reporting period.

Mott MacDonald (2010). Installation of Submarine Gas Pipelines and Associated Facilities from To Kwa Wan to North Point for Former Kai Tak Airport Development: Environmental Monitoring and Audit Manual.

1 INTRODUCTION

ERM-Hong Kong, Limited (ERM) and Mott MacDonald Hong Kong Limited were appointed by the Hong Kong and China Gas Company Limited and McDow-Kaden JV as the Environmental Team (ET) and the Independent Environmental Checker (IEC), respectively, to undertake the Environmental Monitoring and Audit (EM&A) activities for the installation of submarine gas pipelines and associated facilities from To Kwa Wan to North Point for former Kai Tak Airport Development ("the Project").

1.1 PURPOSE OF THE REPORT

This is the 8th Quarterly EM&A Report which summarises the impact monitoring results and inspection/audit findings for the EM&A programme during the reporting period from **1 March to 31 May 2014**.

1.2 STRUCTURE OF THE REPORT

The remainder of the report is structured as follows:

Section 2: Project Information

summarises the background and scope of the Project, works locations, construction programme, construction works undertaken, project organisation and management structure, and the status of Environmental Permit (EP)/licences over the construction phase of the Project.

Section 3: EM&A Requirements

summarises the environmental monitoring and audit requirements including monitoring programmes, monitoring methodologies, monitoring parameters, monitoring frequency, monitoring locations, Action and Limit Levels, Event/Action Plans, environmental mitigation measures as recommended in the approved Environmental Impact Assessment (EIA) report, EP and relevant environmental requirements stated in the Contract Specifications.

Section 4: **Implementation Status on Environmental Mitigation Measures** summarises the implementation of environmental mitigation measures as recommended in the approved EIA report, EM&A Manual, EP and relevant environmental requirements stated in the Contract Specifications.

Section 5: Monitoring Results

summarises the monitoring results obtained in the reporting period and the findings of the weekly site inspection including solid and liquid waste management undertaken within the reporting period.

Section 6: Environmental Non-conformance

summarises and review any non-compliance of environmental performance standard, environmental complaints and environmental summons received within the reporting period.

Section 7: Future Key Issues

summarises the impact forecast and monitoring schedule for the next reporting period.

Section 8: Conclusions

2 PROJECT INFORMATION

2.1 PROJECT BACKGROUND

The Project proposed by the Hong Kong and China Gas Company Limited comprises the construction of a new gas pipeline network from To Kwa Wan to North Point so as to replace the existing one affected by the proposed Cruise Terminal dredging works adjacent to the former Kai Tak runway and the proposed Central Kowloon Route crossing the Kowloon Bay at To Kwa Wan.

The EIA report (*Register No.: AEIAR-153/2010*) for the Project was approved by the Director of Environmental Protection (DEP) on 2 August 2010 under the Environmental Impact Assessment Ordinance (EIAO). Subsequent to the approval of the EIA, an Environmental Permit (EP) (Permit No. EP-401/2010) for the Project was granted by the DEP on 6 October 2010.

2.2 GENERAL SITE DESCRIPTION

The Project involves the construction of the twin submarine gas pipelines across the Victoria Harbour from To Kwa Wan to North Point and the construction of the land gas pipelines and pigging stations for pigging operation at both To Kwa Wan and North Point. The locations of the project areas and stations are presented in *Annex A*.

2.3 PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE

2.3.1 Project Organization

The EM&A programme will require the involvement of the Hong Kong and China Gas Company Limited, an Environmental Team (ET), an Independent Environmental Checker (IEC) and the Contractor. The roles and responsibilities of the various parties involved in the EM&A process have been described in the *EM&A Manual* for this Project and the organization of these parties is presented in *Annex B*.

2.3.2 Key Contact Information

Key contact information of the Project Organization is provided in *Annex B*.

2.4 CONSTRUCTION ACTIVITIES UNDERTAKEN DURING THE REPORTING PERIOD

A summary of the major construction activities undertaken in the reporting period is shown in *Table 2.1*. The locations of the construction activities are shown in *Annex A*. The construction programme of the Project is presented in *Annex C*.

Construction Activities Undertaken

Marine works (Submarine Pipeline):

- Substantial completion of armour rock backfilling from CH0025 to CH3000;
- Completion of reinstatement of granite facing stone at To Kwa Wan cofferdam;
- Completion of repairing works for marine pipeline risers at To Kwa Wan cofferdam;
- Substantial completion of removal of pipe piles and backfilling at To Kwa Wan cofferdam;
- Substantial completion of backfilling of rock mound at North Point cofferdam;
- Completion of reinstatement of seawall blocks at North Point cofferdam;
- Substantial completion of ICCP system installation for 450mm diameter submarine pipeline;
- Substantial completion of extraction of pipe piles at To Kwa Wan cofferdam;
- Substantial completion of backfilling with general fill material at To Kwa Wan cofferdam;
- Substantial completion of reinstatement of granite facing stone with concrete backing at North Point cofferdam;
- Substantial completion of repair works of 450 mm diameter submarine pipeline at North Point cofferdam; and
- Completion of concrete surround of 450 mm diameter submarine pipeline.

Landmains (To Kwa Wan and North Point):

- Completion of reinstatement of North Point Pigging Station;
- Completion of rectification work at San Ma Tau Street Carriageway and Footpath; and
- Commencement of final testing of 600 mm diameter pipeline.

Works Area (To Kwa Wan):

- Completion of the intermediate test of pipeline;
- Substantial completion of installation of ICCP system;
- Completion of concrete surround of the Y-line and the submarine pipelines within To Kwa Wan cofferdam;
- Completion of reinstatement of seawall blocks at To Kwa Wan cofferdam;
- Completion of reinstatement of granite facing stone at To Kwa Wan cofferdam; and
- Substantial completion of extraction of pipe piles at To Kwa Wan cofferdam.

Works Area (North Point):

- Completion of the intermediate test of pipeline;
- Backfilling of armour rock between CH3134 to CH3160;
- Substantial completion of backfilling of rock mound at North Point cofferdam;
- Completion of reinstatement of seawall blocks at North Point cofferdam;
- Substantial completion of reinstatement of granite facing stone at North Point cofferdam; and
- Completion of reinstatement of North Point Pigging Station.

2.5 STATUS OF ENVIRONMENTAL APPROVAL DOCUMENTS

A summary of the valid permits, licences and notifications on environmental protection for this Project is presented in *Table 2.2*.

Table 2.2 Summary of Environmental Licensing, Notification and Permit Status

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Environmental	EP-401/2010	Throughout the	Permit granted on 6
Permit		Contract	October 2010
Notification of	Ref No.	Throughout the	-
Commencement of	1123/01.01/12/	Contract	
Works	0233/L		

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Water Discharge License (North Point)	WT00012521- 2012	Till 31 March 2017	Wastewater discharge licence was issued by EPD on 22 March 2012
Water Discharge License (To Kwa Wan)	WT00012299- 2012	Till 30 April 2017	Wastewater discharge licence was issued by EPD on 25 April 2012
Construction Noise Permit (Marine works)	GW-RE0486-12	Till 17 December 2012; Expired; new permit granted	Issued on 20 June 2012
Construction Noise Permit (Marine works)	GW-RE0976-12	Till 9 March 2013; Expired; new permit granted	Issued on 13 November 2012
Construction Noise Permit (Marine works)	GW-RE0193-13	Till 9 April 2013; Expired; new permit granted	Issued on 1 March 2013
Construction Noise Permit (Marine works)	GW-RE0313-13	Till 9 August 2013; Expired; new permit granted	Issued on 27 March 2013
Construction Noise Permit (Marine works)	GW-RE0570-13	Till 25 July 2013; Expired; new permit granted	Issued on 15 June 2013
Construction Noise Permit (Marine works)	GW-RS0761-13	Till 11 September 2013	Issued on 10 July 2013
Construction Noise Permit (Marine works)	GW-RE1014-13	Till 16 December 2013	Issued on 18 September 2013
Construction Noise Permit (Marine works)	GW-RS1115-13	Till 31 December 2013	Issued on 10 October 2013
Construction Noise Permit (Marine works)	GW-RE0069-14	Till 30 April 2014; Expired; new permit granted	Issued on 20 January 2014
Construction Noise Permit (Marine works)	GW-RE0391-14	Till 31 October 2014	Issued on 8 April 2014
Chemical Waste Producer Registration	5213-244-M2830- 01	Throughout the Contract	Licence approved on 17 February 2012
Marine Dumping Permit (Sediment Type 1, Cheung Chau South)	EP/MD/12-125	Till 14 November 2012; Expired; new permit granted	Issued on 15 May 2012
Marine Dumping Permit (Sediment Type 1, Cheung Chau South)	EP/MD/13-102	Till 17 June 2013; Expired; new permit granted	Issued on 17 December 2012
Marine Dumping Permit (Sediment Type 1, Cheung Chau South)	EP/MD/14-028	Till 25 December 2013	Issued on 26 June 2013
Marine Dumping Permit (Sediment Type 1, East Ninepin)	EP/MD/13-012	Till 30 September 2012; Expired	Issued on 29 May 2012

Permit/ Licences/ Notification	Reference	Validity Period	Remarks
Marine Dumping Permit (Sediment Type 2, East Sha Chau)	EP/MD/13-023	Till 17 July 2012; Expired; new permit granted	Issued on 15 June 2012
Marine Dumping Permit (Sediment Type 2, East Sha Chau)	EP/MD/13-042	Till 17 August 2012; Expired; new permit granted	Issued on 17 July 2012
Marine Dumping Permit (Sediment Type 2, East Sha Chau)	EP/MD/13-054	Till 20 September 2012; Expired; new permit granted	Issued on 20 August 201
Marine Dumping Permit (Sediment Type 2, East Sha Chau)	EP/MD/13-078	Till 8 November 2012; Expired; new permit granted	Issued on 8 October 2012
Marine Dumping Permit (Sediment Type 2, East Sha Chau)	EP/MD/13-090	Till 8 December 2012; Expired; new permit granted	Issued on 8 November 2012
Marine Dumping Permit (Sediment Type 2, East Sha Chau)	EP/MD/13-136	Till 21 April 2013; Expired; new permit granted	Issued on 21 March 2013
Marine Dumping Permit (Sediment Type 2, East Sha Chau)	EP/MD/14-004	Till 31 May 2013; Expired	Issued on 30 April 2013
Marine Dumping Permit (Sediment Type 3, East Sha Chau)	EP/MD/12-127	Till 8 September 2012; Expired; new permit granted	Issued on 8 August 2012
Marine Dumping Permit (Sediment Type 3, East Sha Chau)	EP/MD/13-067	Till 24 October 2012; Expired;	Issued on 25 September 2012

3.1 MARINE WATER QUALITY MONITORING

3.1.1 Water Quality Parameters

The parameters measured *in situ* were:

- Dissolved Oxygen (DO) (% saturation and mg L-1)
- Salinity (ppt)
- Temperature (°C)
- Turbidity (NTU)

The only parameter to be measured in the laboratory was:

• Suspended solids (SS) (mg L⁻¹)

In addition to the water quality parameters, other relevant data were measured and recorded in Water Quality Monitoring Logs, including monitoring location, time, tidal stages, weather conditions and any special phenomenon or work underway at the construction site that may influence the monitoring results.

3.1.2 Monitoring Equipment

Table 3.1 summaries the equipment used for the water quality monitoring.

Table 3.1Equipment used during the Water Quality Monitoring Programme

Equipment	Model
Global Positioning Device	Garmin etrex 10
Water Depth Detector (Echo sounder)	Speedtech Instrument SM-5A
Water Sampler	1510 Kemmerer Water Sampler
Salinity, DO, Temperature Measuring Meter	YSI Pro 2030
Turbidity Meter	HACH Model 2100Q Turbid Meter

3.1.3 Sampling / Testing Protocol

All *in situ* monitoring instruments were checked, calibrated and certified by the analytical laboratory before use ⁽¹⁾. Responses of sensors and electrodes were checked with certified standard solutions before each use.

Wet bulb calibration for a DO probe was carried out at least once per monitoring day. A zero check in distilled water was performed with the turbidity probe at least once per monitoring day. The probe was calibrated

(1) Baseline water quality monitoring was undertaken by the HOKLAS accredited laboratory ETS-Testconsult Ltd.

with a solution of known NTU. In addition, the turbidity probe was calibrated at least twice per month to establish the relationship between turbidity readings (in NTU) and levels of suspended solids (in mg L⁻¹).

On-site calibration of equipment was also carried out following the "*Guide to On-Site Test Methods for the Analysis of Waters*", BS 1427:1993 to check the responses of sensors and electrodes using certified standard solutions before each use. Sufficient stocks of spare parts were maintained for replacements when necessary. Backup monitoring equipment was made available so that monitoring can proceed uninterrupted even when equipment is under maintenance, calibration etc.

Water samples for SS measurements were collected in high density polythene, packed in ice (cooled to 4 °C without being frozen) and delivered to the analytical laboratory as soon as possible after collection.

3.1.4 Laboratory Measurement and Analysis

Analysis of SS was carried out in a HOKLAS accredited laboratory ⁽¹⁾. Water samples of about 1 L were collected at the monitoring stations for carrying out the laboratory suspended solids determination. The SS determination work started within 24 hours after the collection of the water samples. The SS analyses followed the standard method APHA 2540D with a detection limit of 1 mg L⁻¹ as described in *APHA Standard Methods for the Examination of Water and Wastewater*, 21st Edition, unless specified.

Quality Assurance/ Quality Control (QA/ QC) details (such as blank, spike recovery, number of duplicate samples per batch etc) were provided in *Monthly EM&A Reports* in accordance with requirements of HOKLAS.

3.1.5 Sampling Depths & Replication

Each station was sampled and measurements/ water samples were taken at three depths, namely, 1 m below water surface, mid-depth and 1 m above sea bed, except where the water depth was less than 6 m, the mid-depth station may be omitted. For stations that were less than 3 m in depth, only the mid-depth sample was taken.

For *in situ* measurements, duplicate readings were made at each water depth at each station. Duplicate water samples were collected at each water depth at each station.

3.1.6 Monitoring Locations and Frequency

Impact water quality monitoring was conducted during the marine works period at the monitoring stations listed in *Table 3.2* and shown in *Annex D1*.

(1) Marine water quality monitoring was undertaken by the HOKLAS accredited laboratory ETS-Testconsult Ltd.

Monitoring Station	Area	Easting	Northing
WM1	Tai Wan WSD Seawater Intake	837818.8258	818059.9297
WM2	City Garden	838278.6734	817209.9656
WM3	Provident Centre	838443.5777	817233.5234
WM4	North Point Government Offices	839536.1868	817215.6195
WM5	Quarry Bay WSD Seawater Intake	839781.4231	817107.8097
WM6	Taikoo Place	840026.6594	817000
C1	Control Station	836625.9264	817422.6424
C2	Control Station	836747.9445	816670.1762
C3	Control Station	840810.5828	817825.8986
C4	Control Station	840432.5877	816920.1674

In accordance with the *EM&A Manual*, marine water quality monitoring were conducted at six Water Sensitive Receivers (WM1, WM2, WM3, WM4, WM5 and WM6) as well as four Control stations (C1, C2, C3 and C4) (*Table 3.2*) at a frequency of three times a week during the marine works period for the Project. Monitoring was undertaken at mid-flood and mid-ebb tides during each monitoring day. The interval between two sets of consecutive monitoring was not less than 36 hours.

For scheduling, reference were made to the predicted tides at Quarry Bay, which is the tidal station nearest to the Project Site, published on the website of the Hong Kong Observatory ⁽¹⁾. Schedule for impact monitoring has been submitted to the Contractor, Independent Environmental Checker (IEC), Engineer Representative (ER) and Environmental Protection Department (EPD) prior to the commencement of the monitoring works.

3.1.7 Water Quality Compliance

Water quality monitoring was evaluated against Action and Limit Levels. The proposed Action and Limit Levels which are determined from the baseline water quality monitoring results are shown in *Table 3.3*.

In the event that the levels are exceeded, appropriate actions in the Event and Action Plan (*Annex F1*) should be undertaken and a review of works will be carried out by the Contractor(s).

⁽¹⁾ Hong Kong Observatory (2012) <u>http://www.hko.gov.hk/tide/eQUBtide.htm</u> [Accessed in March 2012]

Parameters	Action Level	Limit Level
DO in mg L-1	WSD Seawater Intakes	Surface and Middle
(Surface, Middle & Bottom)	2 mg L ⁻¹	WSD Seawater Intake
		2 mg L-1
	Other Impact Monitoring	
	Stations	Other Impact Monitoring
	5 percentile of baseline data,	Stations
	i.e. 7.79 mg L ⁻¹	4 mg L ⁻¹ or 1 percentile of
		baseline data, i.e. 7.46 mg L ⁻¹
		Bottom
		Impact Monitoring Stations
		2 mg L ⁻¹ or 1 percentile of
		baseline data, i.e. 7.66 mg L ⁻¹
SS in mg L-1	WSD Seawater Intakes	WSD Seawater Intake
(depth-averaged)	10 mg L-1	10 mg L-1
	Other Impact Monitoring	Other Impact Monitoring
	Stations	Stations
	95 percentile of baseline data, i.e. 5.13 mg L ⁻¹	99 percentile of baseline data, i.e. 5.53 mg L ⁻¹
	or	or
	120% of upstream control	130% of upstream control
	station at the same tide of the	station at the same tide of the
	same day	same day
Turbidity (depth-averaged)	WSD Seawater Intakes	WSD Seawater Intakes
fulblany (deput averaged)	10 NTU	10 NTU
	Other Impact Monitoring	Other Impact Monitoring
	Stations	Stations
	95 percentile of baseline data,	99 percentile of baseline data,
	i.e. 3.71 NTU	i.e. 4.03 NTU
	or	or
	120% of upstream control	130% of upstream control
	station at the same tide of the	station at the same tide of the
	same day	same day

Notes:

- (a) "Depth-averaged" is calculated by taking the arithmetic means of the readings of the three depths.
- (b) For DO measurement, non-compliance occurs when monitoring result is lower than the limits.
- (c) For SS and turbidity, non-compliance of water quality results when monitoring results is higher than the limits.
- (d) All the figures given in the table are used for reference only the EPD may amend the figures whenever necessary.
- (e) The levels of SS, Turbidity and DO were confirmed to be similar amongst monitoring stations by statistical analysis. Therefore, the calculation of Action and Limit Levels was based on baseline monitoring data collected from all monitoring stations and the same set of Action and Limit Levels will be adopted for the *Impact Monitoring Stations* (ie not including the WSD Seawater Intakes and Control Stations).

3.2 AIR-BORNE NOISE MONITORING

3.2.1 Monitoring Location

In accordance with the *EM&A Manual*, monitoring of construction noise impact should be conducted at the designated monitoring stations. The construction noise monitoring location for this Project is listed in *Table 3.6* and is shown in *Annexes E1 and E2*.

Table 3.6Noise Monitoring Location

Monitoring Station	Area	Description
SCH02	To Kwa Wan	CCC Kei To Secondary School
FSQ	North Point	North Point Fire Services Married Quarters

3.2.2 Monitoring Parameter and Frequency

Weekly construction noise monitoring was conducted in accordance with the requirements stipulated in the *EM&A Manual*. Thirteen sets of noise monitoring were carried out within this quarterly reporting period.

The construction noise levels were measured in terms of A-weighted equivalent continuous sound pressure level (L_{eq}) in decibels dB(A). $L_{eq (30min)}$ were used as the monitoring parameter for the period in between 0700 – 1900 hours on normal weekdays. In order to obtain supplementary information for data auditing, two statistical sound levels L_{10} and L_{90} (ie the levels exceeded for 10 and 90 percent of the time, respectively), were also recorded during the monitoring for reference. The measured noise levels were logged every 5 minutes throughout the impact monitoring period.

3.2.3 Action and Limit Levels

The Action and Limit levels for noise monitoring during different monitoring periods are summarised in *Table 3.7*.

Table 3.7Summary of Action and Limit Levels for Construction Noise

Time Period	Action Level	Limit Level (dB(A))
0700-1900 hrs on normal weekdays	When one documented compliant is received	75*
1900-2300 hrs on normal weekdays	When one documented compliant is received	70
Restricted hours (2300-0700 hrs)	When one documented compliant is received	55

Note:

⁴ 70 dB(A) for schools and 65 dB(A) during school examination periods.

3.2.4 Monitoring Equipment and Methodology

Construction noise measurements were conducted in accordance with the calibration and measurement procedures as stated in *Annex – General Calibration and Measurement Procedures* of *Technical Memorandum on Noise from*

Construction Work other than Percussive Piling (GW-TM) issued under the *Noise Control Ordinance (NCO) (Cap. 400).*

The sound level meters and calibrator used for the noise measurement, as listed in *Table 3.8*, complies with IEC 651: 1979 and 804:1985 (Type 1) specification. The calibration certificates of the sound level meters and calibrator were shown in *Monthly EM&A Reports*.

Table 3.8Noise Monitoring Equipment

Monitoring Station	Monitoring Equipment (Sound Level Meter and Calibrator)
SCH02	Rion NL-18 (S/N 00360030), NC-73 (S/N 10997142)
FSQ	Rion NL-31 (S/N 00410224), NC-73 (S/N 10997142)

Immediately prior to and following the noise measurements, the accuracy of the measurement equipment was checked using an acoustic calibrator generating a known sound pressure level at a known frequency.

3.2.5 Event and Action Plan

The Event and Action Plan (EAP) for noise monitoring is presented in *Annex F2*.

IMPLEMENTATION STATUS ON ENVIRONMENTAL MITIGATION MEASURES

The Contractor has implemented environmental mitigation measures and requirements as stated in the EIA Report, EP and *EM&A Manual*. The implementation status during the reporting period is summarised in *Annex G*.

5.1 SITE INSPECTIONS & AUDITS

Weekly site inspections were conducted by representatives of the Contractor and the ET on 6, 13 and 20 March 2014; 3, 10, 17 and 24 April 2014; and 8, 16, 22 and 27 May 2014. In addition, joint site inspections were conducted by the Contractor, the ET, the Resident Engineer (RE) and the IEC on 25 March, 29 April and 27 May 2014.

Major observations during the reporting period were summarised as follows:

6 March 2014

- To Kwa Wan Land-based Site:
 - Two chemical containers were not placed properly in any of those drip trays. The Contractor was reminded to place them properly to avoid the chemicals from contaminating the surrounding soil.
 - Stagnant water was found accumulated in the works site. The Contractor was reminded to fill up the space or to apply mosquito-repellent more regularly.
 - It was observed that trash was dumped randomly in works site. The Contractor was reminded to maintain good house-keeping practice and only dispose of any trash at designated areas in the site.

13 March 2014

- To Kwa Wan Land-based Site:
 - Two chemical containers were not placed properly in any of those drip trays which was already observed in last site audit on 6 March 2014. The Contractor was again reminded to place them properly to avoid the chemicals from contaminating the surrounding soil.
- North Point Land-based Site:
 - Some excavated materials and mud were placed on tarpaulin sheet but were very close to the open gully which led directly to the sea. The Contractor was reminded to cover it more properly or to remove them completely if they would not be used.

20 March 2014

- To Kwa Wan Land-based Site:
 - Some areas of To Kwa Wan Land-based Site were accumulated with stagnant water. The Contractor was advised to make the ground flat to avoid accumulation of stagnant water.
 - Stagnant water was accumulated in one of the trenches where water was not flowing through. The Contractor was advised to spray mosquito-repellent to prevent mosquito from breeding.

25 March 2014

- To Kwa Wan Land-based Site:
 - Trash was seen in the cofferdam. The Contractor was reminded to clean it properly.
 - More sandbags were suggested to be placed along the waterfront or the edge of the cofferdam to prevent mud/sand from running into the sea.
 - Chemical waste containers were not placed in drip tray. The Contractor was reminded to place them properly in drip tray.
 - Recycling bins should be properly labelled.
 - Metal sand in containers should be covered while metal sand on the floor shall be removed.
 - Oil stain was found on the surrounding soil. The Contractor was reminded to dispose of as chemical waste.

3 April 2014

- To Kwa Wan Land-based Site:
 - One of the drip trays where two chemical drums were placed was not plugged by stopper properly. The Contractor was reminded to plug it properly to avoid the surrounding soil being contaminated by chemical and oil.
 - Nozzle was found being placed out of the drip tray. The Contractor was reminded to place it properly inside the drip tray.

10 April 2014

- To Kwa Wan Land-based Site:
 - One of the drip trays was not plugged by stopper properly. The Contractor was reminded to plug it properly to avoid the surrounding soil being contaminated by chemical and oil.
 - Some of the excavated materials were not covered properly by tarpaulin sheet. The Contractor was reminded to cover it completely by the end of the working day.

17 April 2014

- To Kwa Wan Land-based Site:
 - Some of the excavated materials were not covered properly by tarpaulin sheet. The Contractor was reminded to cover it completely by the end of the working day.
 - Stagnant water was found inside a container and recycling bins. The Contractor was reminded to clear it more regularly by appropriate procedures.
 - A chemical waste container was not labelled. The Contractor was reminded to label it properly and store it at designated area.

- To Kwa Wan Land-based Site:
 - Drip tray of a generator was not plugged. The Contractor was asked to remind their site workers to plug it properly at all times.
 - Sand and excavated materials were found very close to the waterfront without any barrier in between. The Contractor was advised to either set a temporary barrier or to move the excavated materials and sand away from the edge of the waterfront to prevent any of them from running into the sea directly.
 - Stagnant water was observed in one of the drip trays. The Contractor was reminded to regularly get rid of the stagnant water in proper way and it should be disposed of as chemical waste.
 - The Contractor was reminded that different kinds of refuse should be sorted properly on site.

29 April 2014

- To Kwa Wan Land-based Site:
 - Stagnant water was observed in one of the drip trays. The Contractor was reminded to clear the stagnant water appropriately and regularly.
 - Excavated materials were not covered properly. The Contractor was reminded either to remove it or to cover it completely.
 - Two of the drip trays were not plugged (two generators). The Contractor was reminded to plug it properly to avoid the surrounding soil being contaminated by chemical and oil.
 - Empty tanks should be flipped over to avoid any water accumulated.
 - Chemical drums were not placed in drip tray.
 - Grabbing of rocks from seabed was observed during site audit when no permit was valid to support such action. The Contractor was urged to communicate and investigate this issue with the subcontractor.
- North Point Site:
 - \circ $\;$ The Contractor was reminded to maintain the silt curtain properly.
 - Planks were observed in the trench. The Contractor was advised to remove any unnecessary items in the trench.
 - An open container containing sand was observed at site without being covered. The Contractor was reminded to cover it properly by tarpaulin sheet.

8 May 2014

- North Point Construction Site:
 - The silt curtain was not enclosed properly. The Contractor was reminded to maintain it properly during marine works.

- To Kwa Wan Land-based Site:
 - Excavated materials were found very close to the waterfront without any barrier in between. The Contractor was advised to either set a temporary barrier or to move the excavated materials away from the edge of the waterfront to prevent any of them from running into the sea directly.

16 May 2014

- North Point Construction Site:
 - The silt curtain was not enclosed properly. The Contractor was reminded to maintain it properly during marine works.
- To Kwa Wan Land-based Site:
 - The Contractor was recommended to place more sandbags or other appropriate measures to reduce surface runoff from entering the sea.
 - Some excavated materials were not covered properly by tarpaulin sheet. The Contractor was reminded to cover them by the end of the day.
 - One of the recycling bins was fully occupied. The Contractor was reminded to clear the recycling bins more frequently.

22 May 2014

- To Kwa Wan Land-based Site:
 - The Contractor was suggested to place sandbags along the waterfront of the construction site or to implement other appropriate measures to avoid surface runoff from entering the sea especially in rainy season.
 - Large amount of stagnant water was accumulated in sedimentation tank. The Contractor was recommended to treat it properly.
 - General refuse was observed to be scattered around on site. The Contractor was reminded to keep good-housing practice at all times.

27 May 2014

- North Point Construction Site:
 - Two chemical containers were placed at the site without any drip tray. The Contractor was reminded to place them properly if they have to be used or remove them from site if not required.
- To Kwa Wan Land-based Site:
 - Two of the drip trays were not being plugged properly. The Contractor was reminded to plug them.
 - Stockpile should be removed if not in use or covered it properly if they were in use.

5.2 MARINE WATER QUALITY MONITORING

In accordance with the requirements described in the *EM&A Manual*, marine water quality monitoring was conducted during periods when marine works were scheduled to be undertaken. Impact monitoring was undertaken three times per week from 1 March to 31 May 2014, except on 19 April during which marine works were not undertaken. During the period of impact monitoring, weather condition was generally fine.

Monitoring results are presented graphically in Annex D2 - D6 and key observations are described below.

DO levels from surface, mid-depth and bottom waters were generally similar amongst Control, Impact and WSD Seawater Intake stations, and DO levels were variable throughout the monitoring period which represented natural background fluctuation in water quality.

Quarterly mean DO levels from surface, mid-depth and bottom waters of Impact Stations were significantly lower than those recorded in Baseline Water Quality Monitoring in March 2012 (p < 0.001). Quarterly mean DO levels from surface, mid-depth and bottom waters of Control Stations were also significantly lower than those recorded in Baseline Water Quality Monitoring in March 2012 (p < 0.001). When comparing quarterly mean DO levels from surface, mid-depth and bottom waters between Impact Stations and Control Stations, no significant difference was found (p > 0.05). Therefore, it is considered that the significantly lower DO levels recorded in this quarterly period (ie compared to the baseline levels) are more likely to be representing natural background fluctuation in water quality rather than indicating any unacceptable water quality impacts from the Project since the lower DO levels were recorded at the Impact Stations as well as the Control Stations, which are far away from the marine works locations that should not be affected by the marine works.

Similar to DO levels, turbidity and SS levels were generally similar amongst all stations and variable throughout the monitoring period. High levels of turbidity and SS were occasionally recorded during both mid-ebb and midflood tides. Such fluctuations were also observed during baseline monitoring and are considered to be sporadic events and characteristic of water quality in this area of Hong Kong.

Quarterly mean turbidity and SS levels of Impact Stations were significantly higher than those recorded in Baseline Water Quality Monitoring in March 2012 (p < 0.01). Quarterly mean turbidity and SS levels of Control Stations were also significantly higher than those recorded in Baseline Water Quality Monitoring in March 2012 (p < 0.001).

Comparison of quarterly mean depth-averaged turbidity levels between Impact and Control Stations indicated that turbidity levels at Impact Stations were higher to those recorded at Control Stations (p < 0.05), but the values at Impact Stations were well below Action and Limit Levels. Therefore, it is considered that the Project did not pose any unacceptable water quality impacts in the vicinity of the area.

Comparison of quarterly mean depth-averaged SS levels between Impact and Control Stations indicated that SS levels at Control Stations were similar to those recorded at Impact Stations (p > 0.05). Therefore, it is considered that the significantly higher SS levels recorded in this quarterly period (ie compared to the baseline levels) are more likely to be representing natural background fluctuation in water quality rather than indicating any unacceptable water quality impacts from the Project since the higher SS levels were recorded at the Impact Stations as well as the Control Stations, which are far away from the marine works locations that should not be affected by the marine works.

A total of thirty-nine (39) exceedances were recorded and dated on 1, 4, 6, 8, 11, 13, 15, 18, 20, 22, 25, 27, 29 and 31 March 2014; 2, 4, 8, 10, 12, 15, 17, 22, 24, 26, 28 and 30 April 2014; and 2, 5, 8, 10, 13, 15, 17, 20, 22, 24, 27, 29 and 31 May 2014. Exceedances in the Action and Limit Levels of surface, mid-depth and bottom DO were observed. It is considered that the exceedances in DO levels are more likely to be representing natural background fluctuation in water quality rather than indicating any unacceptable water quality impacts from the Project since exceedances were recorded when marine works were not being undertaken for the Project (eg during mid-flood tide on 4 March; 17, 27, 29 and 31 May 2014; during mid-ebb tide on 15, 22 and 29 March; 24 and 30 April; 22 May 2014, and during both mid-ebb and mid-flood tides on 1, 6, 11, 13 March; 8 and 15 April; 2 May 2014). In addition, the levels of DO at the Impact Stations where exceedances were recorded were similar to those at the Control Stations, which are far away from the Project area.

Mitigation measures for marine works were implemented properly in accordance with requirements stipulated in the *EIA Report, EP* and *EM&A Manual*. Following the review of monitoring data and marine works details in accordance with the procedures stipulated in the Event and Action Plan of the *EM&A Manual*, these exceedances were considered to be due to natural background variation in water quality characteristic and were unlikely to be due to the Project's marine works activities.

5.3 AIR-BORNE NOISE MONITORING

30-minute construction noise measurements were carried out on 1, 7, 15, 19 and 26 March 2014; 4, 9, 15, 24 and 29 April 2014; and 9, 14, 23 and 28 May 2014 at monitoring station FSQ and on 6, 13, 20 and 27 March 2014; 3, 10, 17, 24 and 30 April 2014; and 8, 15, 22 and 29 May 2014 at monitoring station SCH02 during normal working hours in weekdays of the quarterly period. No exceedances of Action and Limit Levels for noise monitoring during normal working hours were recorded.

The monitoring results together with graphical presentations are presented in Annex E3 - E8. The local impacts observed near the monitoring stations of

SCH02 and FSQ were due to traffic noise from Sung On Street and Island Eastern Corridor, respectively.

5.4 WASTE MANAGEMENT EM&A

Waste generated from this Project includes inert construction and demolition (C&D) materials, non-inert C&D materials. Reference has been made to the Monthly Summary Waste Flow Table prepared by the Contractor (*Annex H*).

The waste statistics provided in this section represent the cumulative quantity of wastes generated from all sites in this Project. With reference to relevant handling records and trip tickets of this Project, the quantities of different types of waste generated in the reporting months of this quarterly period are summarised in *Table 5.1*. The inert C&D materials and general refuse generated from the Project were disposed of at Tseung Kwan O Area 137 Fill Bank and SENT Landfill, respectively.

Table 5.1Quantities of Waste Generated from the Project for all Sites

Month / Year			Quantity			
	C&D Materials	C&D Materials	Chemical	Marine D		
	(inert) ^(a)	(non-inert) ^(b)	Waste	Type 1	Type 2	Type 3
March 2014	37.80 tonnes(c)	4.25 tonnes (d)	0 L	0 m ³	0 m ³	0 m ³
April 2014	0 tonnes	1.07 tonnes (e)	0 L	0 m ³	0 m ³	0 m ³
May 2014	27 tonnes (f)	1.12 tonnes (g)	0 L	0 m ³	0 m ³	0 m ³

Notes:

(a) Inert C&D materials include bricks, concrete, building debris, rubble and excavated soil.

(b) The non-inert C&D materials consisted of general refuse and vegetation/ rubbish.

(c) 37.8 tonnes of inert C&D Materials were generated in March 2014. 30 tonnes were reused in the Contract. 7.8 tonnes were stored as stockpile at site.

- (d) The non-inert C&D materials consisted of 4.25 tonnes of general refuse generated in March 2014.
- (e) The non-inert C&D materials consisted of 1.07 tonnes of general refuse generated in April 2014.
- (f) 27 tonnes of inert C&D Materials were generated and reused in the Contract in May 2014.
- (g) The non-inert C&D materials consisted of 1.07 tonnes of general refuse generated in May 2014.

6 ENVIRONMENTAL NON-COMFORMANCE

6.1 SUMMARY OF ENVIRONMENTAL NON-COMPLIANCE

No non-compliance of EIA / EM&A / EP / legislative requirements was recorded during the reporting period.

6.2 SUMMARY OF ENVIRONMENTAL COMPLAINT

No complaint was received during the reporting period. The cumulative compliant/summons/prosecution log is shown in *Annex I*.

6.3 SUMMARY OF ENVIRONMENTAL SUMMON AND SUCCESSFUL PROSECUTION

No summons/ prosecution was received during the reporting period. The cumulative compliant/summons/prosecution log is shown in *Annex I*.

7.1 CONSTRUCTION ACTIVITIES FOR THE COMING QUARTER

Works to be undertaken for the coming reporting quarter are summarised in *Table 7.1.*

Table 7.1Construction Works to be undertaken in the Coming Quarter

W	ork to be taken
•	Installation of ICCP system and its accessories;
•	Armour rock backfilling;
•	Seawall reinstatement; and
•	Final testing.

Potential environmental impacts arising from the above construction activities are mainly associated with dust, construction noise, site runoff, marine water quality and waste management issues. The updated construction programme for the Project is presented in *Annex C*.

7.2 SOLID AND LIQUID WASTE MANAGEMENT STATUS

As the major construction works in the coming quarter are armour rock backfilling and seawall reinstatement, waste generated from this Project for the coming quarter will include inert and non-inert C&D materials. Part of the inert C&D materials will be stockpiled on site for reuse and the remaining will be disposed of at Tseung Kwan O Area 137 Fill Bank. Chemical waste will be stored at designated area and collected by a licensed collector. Surface runoff, sewage and wastewater will be reduced using proper site management such as the use of sedimentation tanks with sufficient capacity, vehicle and plant cleaning before leaving a construction site, etc (detailed in *Annex G*). General refuse generated from the Project will be disposed of SENT Landfill.

This 8th Quarterly EM&A Report presents the EM&A programme undertaken during the reporting period from 1 March to 31 May 2014 in accordance with *EM&A Manual* and requirements of the EP (EP-401/2010).

Marine works were undertaken during this quarterly period and construction phase water quality monitoring was conducted in accordance with the requirements described in the *EM&A Manual*. Exceedances of Action and Limit Levels for water quality were recorded in thirty-nine (39) monitoring events from 1 March to 31 May 2014. It is considered that the exceedances were sporadic events and represented natural background fluctuation in water quality.

30-minute construction noise measurements were carried out at the monitoring stations SCH02 and FSQ during normal weekdays of the reporting period. No exceedance of Action or Limit Level was recorded during the reporting period.

Weekly site inspections were conducted in the reporting period. Joint site inspections were conducted on 25 March, 29 April and 27 May 2014 by the Contractor, the ET, the RE and the IEC. Most of the mitigation measures recommended in the EIA/ *EM&A manual*/ EP were implemented by the Contractor. Follow-up actions for the observed environmental deficiency during the site inspections were taken as reported by the Contractor and observed in the next weekly site inspection conducted.

No non-compliance event was recorded during the reporting period.


No complaint and summons/prosecution was received during the reporting period.

The EM&A programme is considered effective in reflecting the environmental conditions at the site. The site inspection results also indicated that the Project has no unacceptable environmental impacts and the mitigation measures were effectively implemented. The ET will keep track of the EM&A programme to ensure compliance of environmental requirements and the proper implementation of all necessary mitigation measures in the coming periods.

Change to the monitoring programme is not considered to be necessary at this stage. The monitoring programme will be evaluated as appropriate in the next reporting period.

Annex A


Locations of Works Areas

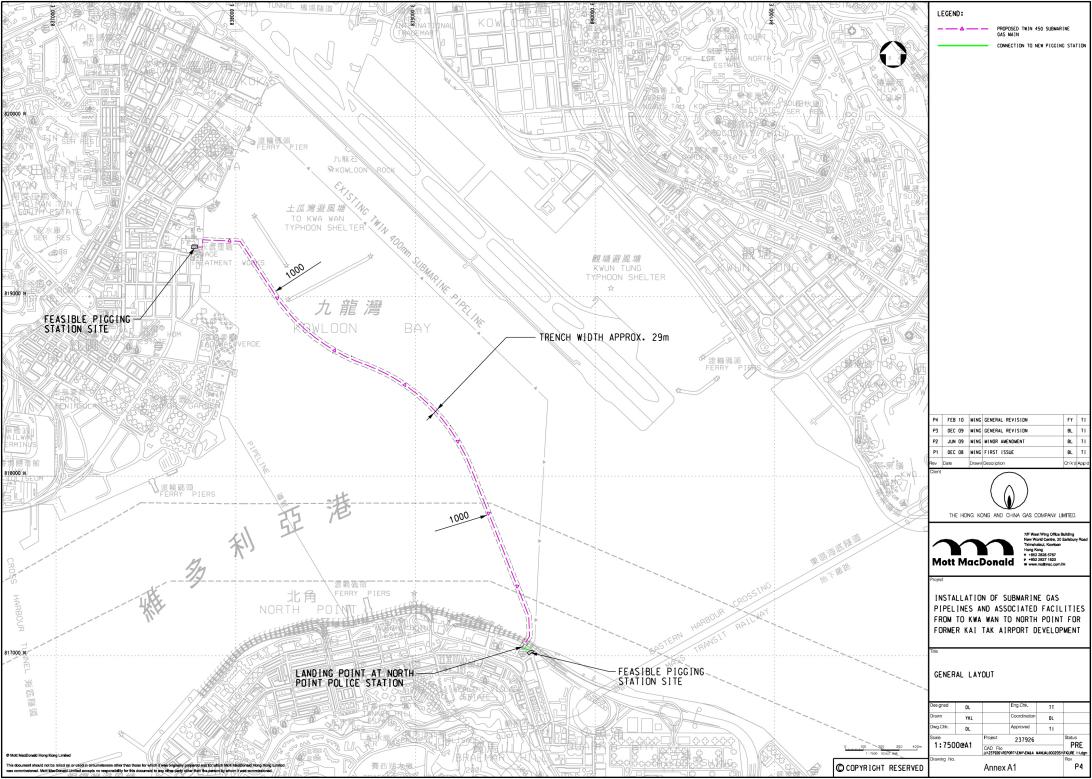

Annex B

Project Organization Chart and Contact Details



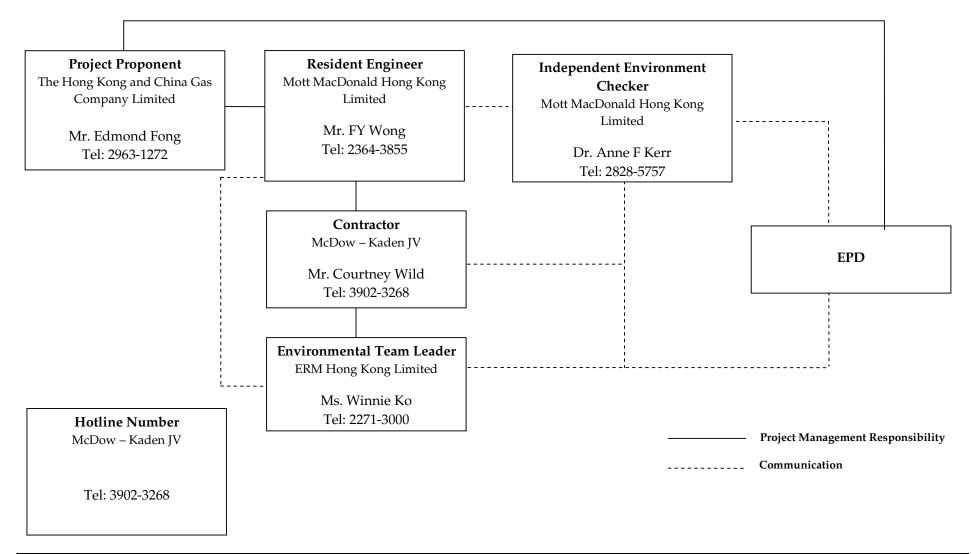

ENVIRONMENTAL RESOURCES MANAGEMENT

Annex C

Construction Programme


Project Ref. No.: GSPD/SP/TKW-NP/089/2011

UPDATED MASTER PROGRAMME REV. 27

Installation of Submarine Gas Pipelines and Associated Facilities From To Kwa Wan to North Point for Former Kai Tak Airport Development

Progress Report as of 20 March 2014

		Activity Name		Early Finish	Late Start	Late Finish	Float		Dec. lo	n Feb	Mar	or Me	2012 V Jun		Sen		ec Jan	eb Mer	Anr	av Jup	J13
wna	as - Subma	rine and Land Gas Pipelines Project		20-Oct-14	02-Jan-13	20-Oct-14			Dec Ja	n Feb	Mar 7	tpr wia	y Jun .	Jui Aug	Sep		sc Jan r	ed Mar	Apr M	ay Jun	Jui
	ct Key Date		1021 04-Jan-12 A	03-Jul-14	03-Jun-13	03-Jul-14	0	89.63%										<u> </u>	<u> </u>	<u> </u>	<u> </u>
			200, 04- Jap-12 A	20-Son-12 A				100%													
roje		for Commencement of Works		29-3ep-12 A																	
		Project Commencement							×.												
		Possession of Portion A1, A2, C, E and F Possession of Portion D							≬										++		<u> </u>
		Arrival of Pipeline Sections by HKCG									•				•						
roie		for Completion of Works		03-Jul-14	03-Jun-13	03-Jul-14	0	83.42%								Ť.	-		÷		<u> </u>
	-	Completion of Trench Dredging	0	12-Jan-13 A				100%									•				
		Completion of Pipe Laying for Submarine Gas	0					100%									Ť				
		Completion of Pipe Testing for Submarine Pipeline before Backfilling	0					100%											1		<u> </u>
	TG-KD-C-F-1035	Completion of All Works in Portion C and Handover of Portion C to pigging station contractor	0	06-Mar-14 A				100%													
	TG-KD-C-F-1040	Completion of Backfilling for Submarine Gas Pipelines	0	20-Mar-14*		03-Jun-13	-289	0%													
	TG-KD-C-F-1045	Completion of Reinstatement of Seawall and other Existing Features	0	20-Mar-14*		03-Jun-13	-289														
		Early Completion of All Works in To Kwa Wan Works Area Portion A1 if all Permits are Approved by 90 Days	0			19-Jun-13															ļ
		Early Completion of All Works in North Point Works Area Portion D, E and F if all Permits are Approved by 90 Days	0			19-Jun-13															
		Early Completion of Submarine Gas Pipelines including Final Testing if all Permits are Approved by 90 Days	0																		
	TG-KD-C-F-1090 TG-KD-C-F-1260	Early Completion of Portion C1 Land Gas Pipelines if all Permits are Approved by 90 Days Late Completion of All Works in To Kwa Wan Works Area Portion A1 if all Permits are not Approved by 90 Days	0																		
	TG-KD-C-F-1280	Late Completion of All Works in North Point Works Area Portion A Lift all Permits are not Approved by 90 Days	0																		
	TG-KD-C-F-1300	Late Completion of Submarine Gas Pipelines including Final Testing if all Permits are not Approved by 90 Days	0	20-Mar-14*		03-Jul-13	-259	0%											+		+
	TG-KD-C-F-1340	Late Completion of Portion C1 Land Gas Pipelines if all Permits are not Approved by 90 Days	0	20-Mar-14*		03-Jul-13	-259	0%													
		Completion of Portion C2 Land Gas Pipelines	0					100%													
	TG-KD-C-F-1410	Completion of Project Video	0	20-Oct-13 A				100%													
	TG-KD-C-F-1420	Early Completion of Maintenance Period for Portions A1, A2, B, C1, D, E and F	0	19-Jun-14*		19-Jun-14	0	0%													
	TG-KD-C-F-1430	Late Completion of Maintenance Period for Portions A1, A2, B, C1, D, E and F	0	03-Jul-14*		03-Jul-14	0	0%				1									
	TG-KD-C-F-1460	Completion of Maintenance Period for Portion C2	0					100%													
est	tone Dates		990 31-Jan-12 A	20-Oct-14	02-Jan-13	20-Oct-14	0	78.3%													
ost	Centre A		990 31-Jan-12 A	20-Oct-14	18-Jan-14	20-Oct-14	0	78.3%				-				++	++	+	 	+	+
	TG-CC-A-M-0002	On completion of the provision of the Enigneer's principal office for occupation and use	0	19-May-12 A				100%					.								
		On completion of the provision of the Enigneer's secondary office for occupation and use	0	14-Apr-12 A				100%			۰	•							+		
	TG-CC-A-M-0004	Provide all necessary documentation that the third party insurance has been effected	0	03-Feb-12 A				100%		•		•									
	TG-CC-A-M-0005	Provide all necessary documentation that the professional indemnity insurance has been effected	0	31-May-12 A				100%				0	•								
	TG-CC-A-M-0006	Provide all necessary documentation that the care of the Works insurance has been effected	0	03-Feb-12 A				100%		8											
	TG-CC-A-M-0007	Provide all necessary documentation that the employees' compensation insurance has been effected	0	31-Jan-12 A				100%		• •											
	TG-CC-A-M-0008	Provide all necessary documentation that the surety bond has been effected	0									8									
		On acceptance of all land transport delivered for the use of the Engineer	0							^											
		On acceptance of all marine transport delivered for the use of the Engineer On completion of installation of the Contract Computer Facilities for the use of the Engineer	0									•									
		On completion of all hoardings, temporary fences, gates and signboards	0										۱								
		On acceptance of Safety Plan	0							8											+
		On acceptance of Environmental Management Plan	0					100%			^										
	TG-CC-A-M-0015	On completion of all Welding Procedure Qualification Tests	0	18-Oct-12 A				100%								• 💊					
	TG-CC-A-M-0016	On completion of condition surveys for existing TKW Sewage Outfall, existing bridge at IEC and Existing Seawalls	0	20-Mar-12 A				100%			•	۰	,								
	TG-CC-A-M-0017	On completion of general site clearance of the Site	0	25-Feb-12 A				100%		•	٥										
		Satisfactory fulfilment of all obligations & completion of all activities expressly covered for the period of 3 mths	0					100%			8										
	TG-CC-A-M-0019	Satisfactory fulfilment of all obligations & completion of all activities expressly covered for the period of 6 mths	0	04-Jul-12 A				100%					8								
		Satisfactory fulfilment of all obligations & completion of all activities expressly covered for the period of 9 mths	U													•	•				
	TG-CC-A-M-0021 TG-CC-A-M-0022	Satisfactory fulfilment of all obligations & completion of all activities expressly covered for the period of 12 mths Satisfactory fulfilment of all obligations & completion of all activities expressly covered for the period of 15 mths	0															•	*		
	TG-CC-A-M-0022	Issuance of the certificates of completion of the Works under Cost Centres B, C1 and D plus all works under Portion A	0																ř		+
	TG-CC-A-M-0024	Completion of all activities 3 mths commencement of the Maintenance Period of the Works for Cost Centres A, B, C1 and D	0			18-Jan-14	-60	0%													
		Completion of all activities 3 mths commencement of the Maintenance Period of the Works for Cost Centre C2	0					100%													
	TG-CC-A-M-0026	Completion of all activities 3 mths commencement of the Maintenance Period of the Works for Cost Centre of All Section	0	20-Mar-14*		18-Jan-14	-60	0%													
	TG-CC-A-M-0027	Completion of all activities 6 mths commencement of the Maintenance Period of the Works for Cost Centres A, B, C1 and D	0	18-Apr-14*		18-Apr-14	0	0%													
	TG-CC-A-M-0028	Completion of all activities 6 mths commencement of the Maintenance Period of the Works for Cost Centre C2	0	03-Mar-14 A				100%													Π
		Completion of all activities 6 mths commencement of the Maintenance Period of the Works for Cost Centre of All Section	0	18-Apr-14*		18-Apr-14	0	0%													
		Completion of all activities 9 mths commencement of the Maintenance Period of the Works for Cost Centres A, B, C1 and D	0	17-Jul-14*		17-Jul-14	0	0%													
		Completion of all activities 9 mths commencement of the Maintenance Period of the Works for Cost Centre C2	0			47 1 1 1 1	-	100%													
		Completion of all activities 9 mths commencement of the Maintenance Period of the Works for Cost Centre of All Section	0			17-Jul-14	0								ļ				<u> </u>		
	TG-CC-A-M-0033 TG-CC-A-M-0034	Issuance of the certificates of completion of the Works under Cost Centre C2 Issuance of the maintenance certificate for the Works under Cost Centres B, C1 and D plus all works under Portion A	U			20. Jun-14	0														
	TG-CC-A-M-0034	Issuance of the maintenance certificate for the all Works for under Cost Centres B, C I and D plus all works under Portion A Issuance of the maintenance certificate for the all Works for under Cost Centre C2 plus other remaining works	0			20-3011-14	U														
	TG-CC-A-M-0036	Issuance of the maintenance certificate of all Section(s) of the Works by the Engineer	0	20-Oct-14*		20-Oct-14	0	0%													
ost	Centre B		699 20-Mar-12 A	20-Mar-14	04-Mar-13			100%			÷		1 1	-		++			-		
		On submission of method statement for hydrographic / geophysical surveys	0	20-Mar-12 4				100%			•								+		<u> </u>
		On acceptance of method statement for hydrographic / geophysical surveys	0					100%				*									
	Remaining	evel of Effort Actual Work Critical Remaining Work	♦ Milestone										F	Page 1	of 6						

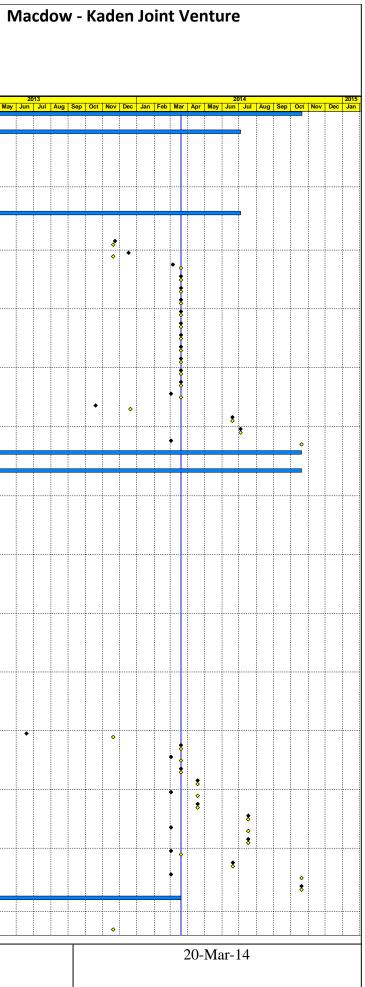


Installation of Submarine Gas Pipelines and Associated Facilities From To Kwa Wan to North Point for Former Kai Tak Airport Development

UPDATED MASTER PROGRAMME REV. 27

Progress Report as of 20 March 2014

	Activity Name	Original Early	Start Early Finish Late		Complete Dec. 1	ob Mar	Apr. Mary	2012	Aug		av Dea	Eab Mar	Apr. May 1	-
TG	-CC-B-M-0038 On completion of pre-commencement survey	Duration	19-Apr-12 A	Float	Complete Dec Jan I 100%	ed Mar	Apr May	Jun Jul	Aug Se	p Oct No	v Dec Jan	<mark>1 Feb Mar</mark>	Apr May Ju	<u>.</u>
	-CC-B-M-0039 On submission of method statement for dredging	0	28-May-12 A		100%		8							
	-CC-B-M-0040 On acceptance of method statement for dredging	0	09-Jul-12 A		100%		Ĭ	•						
	-CC-B-M-0041 On completion of 10% for the total volume of dredging	0	03-Jul-12 A		100%			•				+		
	-CC-B-M-0042 On completion of 20% for the total volume of dredging	0	20-Jul-12 A		100%			`						
	-CC-B-M-0043 On completion of 30% for the total volume of dredging	0	03-Aug-12 A		100%			•	• 。					
	-CC-B-M-0044 On completion of 40% for the total volume of dredging	0	17-Aug-12 A		100%				×.					
	-CC-B-M-0045 On completion of 50% for the total volume of dredging	0	04-Sep-12 A		100%				•	•				
	-CC-B-M-0046 On completion of 60% for the total volume of dredging	0	13-Sep-12 A		100%				•	•		++		
	-CC-B-M-0047 On completion of 70% for the total volume of dredging	0	02-Oct-12 A		100%					*• <u> </u>				
	-CC-B-M-0048 On completion of 80% for the total volume of dredging	0	16-Nov-12 A		100%					, ľ,	•			
	-CC-B-M-0049 On completion of 90% for the total volume of dredging	0	04-Dec-12 A		100%						•			
		0									♦.			
		0	12-Jan-13 A		100%						•			
	-CC-B-M-0051 Completion of trench dredging on or before the target completion date as specified in the Contract	0	12-Jan-13 A		100%						••			
	-CC-B-M-0052 On acceptance of post-dredging survey	0	17-Mar-13 A		100%							8		
ΤG	-CC-B-M-0053 On submission of method statement for submarine pipe laying	0	07-Jun-12 A		100%			•						
ΤG	-CC-B-M-0054 On acceptance of method statement for submarine pipe laying	0	05-Aug-13 A		100%									
TG	-CC-B-M-0055 On completion of establishment of submarine pipe laying equipment for Section 1 of the submarine pipeline	0	27-May-13 A		100%								•	<
TG	-CC-B-M-0056 On completion of establishment of submarine pipe laying equipment for Section 2 of the submarine pipeline	0	11-Jan-13 A		100%						•			<
TG	-CC-B-M-0057 On completion of establishment of submarine pipe laying equipment for Section 3 of the submarine pipeline	0	11-Jan-13 A		100%						•			0
TG	CC-B-M-0058 On completion of establishment of submarine pipe laying equipment for Section 4 of the submarine pipeline	0	31-Aug-13 A		100%									
	-CC-B-M-0059 On completion of laying of 5% for the total length of 2 x 450mm submarine pipeline	0	23-Mar-13 A		100%							8		
	-CC-B-M-0060 On completion of laying of 10% for the total length of 2 x 450mm submarine pipeline	0	27-Mar-13 A		100%									
	-CC-B-M-0061 On completion of laying of 15% for the total length of 2 x 450mm submarine pipeline	0	29-Mar-13 A		100%				+					
		0										•		
	-CC-B-M-0062 On completion of laying of 20% for the total length of 2 x 450mm submarine pipeline	0	01-Apr-13 A		100%							•	,	
	-CC-B-M-0063 On completion of laying of 25% for the total length of 2 x 450mm submarine pipeline	U	04-Apr-13 A		100%							•		
	-CC-BM-0064 On completion of laying of 30% for the total length of 2 x 450mm submarine pipeline	0	08-Apr-13 A		100%							♦		
	-CC-B-M-0065 On completion of laying of 35% for the total length of 2 x 450mm submarine pipeline	0	10-Apr-13 A		100%							♦ 1		
TG	-CC-B-M-0066 On completion of laying of 40% for the total length of 2 x 450mm submarine pipeline	0	13-Apr-13 A		100%							♦	•	
TG	-CC-B-M-0067 On completion of laying of 45% for the total length of 2 x 450mm submarine pipeline	0	16-Apr-13 A		100%							•	•	
TG	-CC-B-M-0068 On completion of laying of 50% for the total length of 2 x 450mm submarine pipeline	0	18-Apr-13 A		100%							•	•	
TG	-CC-B-M-0069 On completion of laying of 55% for the total length of 2 x 450mm submarine pipeline	0	20-Apr-13 A		100%							•	•	
TG	-CC-B-M-0070 On completion of laying of 60% for the total length of 2 x 450mm submarine pipeline	0	22-Apr-13 A		100%								8	
TG	-CC-B-M-0071 On completion of laying of 65% for the total length of 2 x 450mm submarine pipeline	0	25-Apr-13 A		100%									
	-CC-B-M-0072 On completion of laying of 70% for the total length of 2 x 450mm submarine pipeline	0	28-Apr-13 A		100%									
	-CC-B-M-0073 On completion of laying of 75% for the total length of 2 x 450mm submarine pipeline	0	30-Apr-13 A		100%									
	-CC-B-M-0074 On completion of laying of 80% for the total length of 2 x 450mm submarine pipeline	0	02-May-13 A		100%								, i i i i i i i i i i i i i i i i i i i	
		0			100%								°.	
	-CC-B-M-0075 On completion of laying of 85% for the total length of 2 x 450mm submarine pipeline	0	05-May-13 A										•	
	-CC-BM-0076 On completion of laying of 90% for the total length of 2 x 450mm submarine pipeline	0	10-Jun-13 A		100%									•
	-CC-B-M-0077 On completion of laying of 95% for the total length of 2 x 450mm submarine pipeline	0	28-Jun-13 A		100%									<
	-CC-B-M-0078 On completion of laying of 100% for the total length of 2 x 450mm submarine pipeline	0	31-Aug-13 A		100%									
TG	-CC-B-M-0079 Completion of pipe laying of submarine gas pipelines on or before the target completion date	0	30-Aug-13 A		100%									
TG	-CC-B-M-0080 Completion of pipe testing of submarine gas pipelines before backfilling on or before the target completion date	0	17-Dec-13 A		100%									
TG	-CC-B-M-0081 On submission of method statement for backfilling	0	18-May-13 A		100%								•	0
TG	-CC-B-M-0082 On acceptance of method statement for backfilling	0	07-Jun-13 A		100%								•	*
TG	-CC-B-M-0083 On completion of 10% for the total volume of backfilling	0	03-Oct-13 A		100%									
TG	-CC-B-M-0084 On completion of 20% for the total volume of backfilling	0	12-Oct-13 A		100%									
TG	CC-B-M-0085 On completion of 30% for the total volume of backfilling	0	20-Oct-13 A		100%									
	-CC-B-M-0086 On completion of 40% for the total volume of backfilling	0	30-Oct-13 A		100%				+					
	-CC-B-M-0086 On completion of 40% for the total volume of backfilling	0	20-Nov-13 A		100%									
		0												
	-CC-B-M-0088 On completion of 60% for the total volume of backfilling	U	30-Nov-13 A		100%									
	-CC-B-M-0089 On completion of 70% for the total volume of backfilling	0	20-Dec-13 A		100%									
	CC-B-M-0090 On completion of 80% for the total volume of backfilling	0	20-Jan-14 A		100%									
TG	-CC-B-M-0091 On completion of 90% for the total volume of backfilling	0	20-Mar-14*	17-Apr-13 -336	0%									
TG	-CC-B-M-0092 On completion of 100% for the total volume of backfilling	0	20-Mar-14*	02-May-13 -321	0%									
TG	-CC-B-M-0093 On acceptance of post-backfilling survey	0	20-Mar-14*	28-May-13 -295	0%									
	-CC-B-M-0094 On submission of method statement for cofferdam at To Kwa Wan	0	18-Jun-12 A		100%			•						
	-CC-B-M-0095 On acceptance of method statement for cofferdam at To Kwa Wan	0	12-Nov-12 A		100%					•	•			
	-CC-B-M-0096 On completion of excavation at To Kwa Wan	0	23-Mar-13 A		100%				+		÷++	•		
	-CC-B-M-0097 On completion of excavation at 10 Kwa Wan	0	23-Nov-13 A		100%									0
		0												
	-CC-B-M-0098 On completion of permanent reinstatement at To Kwa Wan	U	23-Nov-13 A		100%									
	-CC-B-M-0099 Completion of all works in To Kwa Wan Works Area (Portion A1)	0	23-Nov-13 A		100%			•						
	-CC-B-M-0100 On submission of method statement for cofferdam at North Point	0	18-Jun-12 A		100%			•	 					
TG	-CC-B-M-0101 On acceptance of method statement for cofferdam at North Point	0	12-Nov-12 A		100%					•	`			
TG	-CC-B-M-0102 On completion of excavation at North Point	0	23-Nov-13 A		100%									
TG	-CC-B-M-0103 On completion of main laying at North Point	0	23-Nov-13 A		100%									
TG	-CC-B-M-0104 On completion of permanent reinstatement at North Point	0	20-Mar-14*	04-Mar-13 -380	0%									
	-CC-B-M-0105 Completion of all works in North Point Works Area (Portion C)	0	20-Mar-14*	03-Apr-13 -350	0%									
	-CC-B-M-0106 Completion of backfilling of pipelines, reinstatement of seawalls &existing features on or before target completion date	0	20-Mar-14*	02-May-13 -321	0%				+					
	-CC-B-M-0107 On submission of method statement for cathodic protection	0	14-Dec-12 A	02 may 10 021	100%						•			
10		U	14-Dec-12 A		100 /0			1			<u> </u>			
				1				-						
								Da	ge 2 o	オド				
R	emaining Level of Effort Actual Work Critical Remaining Work	Milesto	ne					īα	90 Z 0	10				

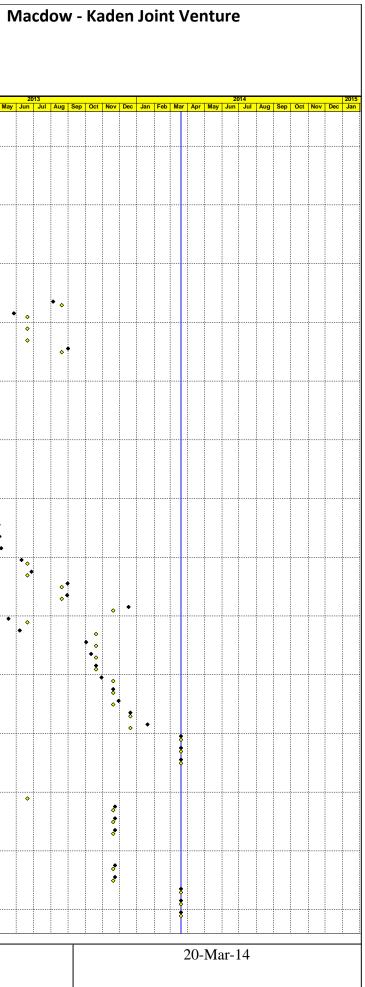


Project Ref. No.: GSPD/SP/TKW-NP/089/2011

Installation of Submarine Gas Pipelines and Associated Facilities From To Kwa Wan to North Point for Former Kai Tak Airport Development

UPDATED MASTER PROGRAMME REV. 27

Progress Report as of 20 March 2014

TG-CC-B-M-0108 On acceptance of method statement for cathodic protection	Original Early Start Duration 0	Carly Finish Late Sta			mplete De 100%	ec Jan	Feb Mar	Apr M	lay Jun	Jul Aug S	ep Oct	Nov Dec	Jan Feb Mar	Apr May J
TG-CC-B-M-0108 On acceptance of methodo statement for cathodic protection TG-CC-B-M-0109 On completion of installation for cathodic protection	0	04-Sep-13 A 20-Mar-14*	10-Apr-13		100% 0%									
TG-CC-B-M-010 On completion of testings for cathodic protection	0	04-Sep-13 A	10-Api-13		100%									
TG-CC-B-M-0111 Completion of final pipe testing (excluding intelligent pigging inspection) for submarine gas pipelines & reinstatement	0	20-Mar-14*	28-May-13		0%									
TG-CC-B-M-0112 On completion of the whole of the works under this Cost Centre to the satisfaction of the Engineer	0	20-Mar-14*			0%									
	485 05-Nov-12		-		100%									
Centre C1														
TG-CC-C1-M-0113 On completion of 10% for the total length of trench excavation	U	05-Nov-12 A 18-Jan-13 A			100% 100%							•	•	
TG-CC-C1-M-0114 On completion of 20% for the total length of trench excavation	0												<u>ک</u>	
TG-CC-C1-M-0115 On completion of 30% for the total length of trench excavation	0	05-Feb-13 A			100%								• ♦	
TG-CC-C1-M-0116 On completion of 40% for the total length of trench excavation	0	04-Apr-13 A			100%									• •
TG-CC-C1-M-0117 On completion of 50% for the total length of trench excavation	0	30-Sep-13 A			100%									
TG-CC-C1-M-0118 On completion of 60% for the total length of trench excavation	0	31-Oct-13 A			100%									
TG-CC-C1-M-0119 On completion of 70% for the total length of trench excavation TG-CC-C1-M-0120 On completion of 80% for the total length of trench excavation	0	20-Nov-13 A 17-Jan-14 A			100% 100%									
TG-CC-C1-M-0120 On completion of 90% for the total length of trench excavation	0	22-Jan-14 A			100%									
TG-CC-C1-M-0122 On completion of 100% for the total length of trench excavation	0	22-Jan-14 A 20-Mar-14*	02-Feb-13		0%									
TG-CC-C1-M-0122 On completion of 10% for the total length of pipelaying and mechanical works	0	04-Dec-12 A	02-1 60-13		100%									
TG-CC-C1-M-0123 On completion of 20% for the total length of pipelaying and mechanical works	0	19-Jan-13 A			100%							•	•	
TG-CC-C1-M-0125 On completion of 30% for the total length of pipelaying and mechanical works	0	06-Feb-13 A			100%								•	
TG-CC-C1-M-0126 On completion of 40% for the total length of pipelaying and mechanical works	0	10-Apr-13 A			100%								• •	•
TG-CC-C1-M-0127 On completion of 50% for the total length of pipelaying and mechanical works	0	30-Sep-13 A			100%									•
TG-CC-C1-M-0127 On completion of 50% for the total length of pipelaying and mechanical works TG-CC-C1-M-0128 On completion of 60% for the total length of pipelaying and mechanical works	0	30-Sep-13 A 31-Oct-13 A			100%									
TG-CC-C1-M-0128 On completion of 60% for the total length of pipelaying and mechanical works TG-CC-C1-M-0129 On completion of 70% for the total length of pipelaying and mechanical works	0	20-Nov-13 A			100%									
TG-CC-C1-M-0129 On completion of 70% for the total length of pipelaying and mechanical works TG-CC-C1-M-0130 On completion of 80% for the total length of pipelaying and mechanical works	0	20-1NOV-13 A 17-Jan-14 A			100%									
TG-CC-C1-IN-0130 On completion of 90% for the total length of pipelaying and mechanical works	0	20-Jan-14 A			100%									
TG-CC-C1-M-0131 On completion of 90% for the total length of pipelaying and mechanical works	0	20-Jan-14 A 20-Jan-14 A			100%									
TG-CC-C1-M-0132 On completion of 100% for the total length of permanent reinstatement	0	20-Jan-14 A 04-Dec-12 A			100%							•		
TG-CC-C1-M-0133 On completion of 10% for the total length of permanent reinstatement	0	21-Jan-13 A			100%							•	•	
TG-CC-C1-M-0135 On completion of 30% for the total length of permanent reinstatement	0	07-Feb-13 A			100%			·····					•	
TG-CC-C1-M-0136 On completion of 40% for the total length of permanent reinstatement	0	13-Apr-13 A			100%								×	•
TG-CC-C1-M-0137 On completion of 50% for the total length of permanent reinstatement	0	30-Sep-13 A			100%									`
TG-CC-C1-M-0138 On completion of 60% for the total length of permanent reinstatement	0	31-Oct-13 A			100%									
TG-CC-C1-M-0139 On completion of 70% for the total length of permanent reinstatement	0	20-Dec-13 A			100%									
TG-CC-C1-M-0139 On completion of 80% for the total length of permanent reinstatement	0	20-Dec-13 A			100%									
TG-CC-C1-M-0140 On completion of 90% for the total length of permanent reinstatement	0	20-Jan-14 A			100%									
TG-CC-C1-M-0142 On completion of 100% for the total length of permanent reinstatement	0	20-Jan-14 A 20-Mar-14*	11-Mar-13	-373	0%									
TG-CC-C1-M-0142 On completion of all cathodic protection works	0	20-Mar-14 20-Mar-14*	27-Mar-13	-373	0%									
TG-CC-C1-M-0143 On completion of all califold protection works TG-CC-C1-M-0144 On completion of final air testing to the satisfaction of the Engineer	0	20-Mar-14 20-Mar-14*	27-Mar-13 19-Mar-13	-357	0%									
TG-CC-C1-M-0144 On completion of hind all esting to the satisfaction of the Engineer	0	20-Mar-14 20-Mar-14*	27-Mar-13	-303	0%									
TG-CC-C1-M-0146 On completion of vacuum drying to the satisfaction of the Engineer	0	20-Mar-14*	05-Apr-13	-348	0%									
TG-CC-C1-M-0147 On completion of the whole of the works under this Cost Centre to the satisfaction of the Engineer	ů.	20-Mar-14*	15-May-13	-308	0%									
	393 08-Dec-12		-		100%									
TG-CC-C2-M-0148 On completion of 10% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0149 On completion of 20% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0150 On completion of 30% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0151 On completion of 40% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0152 On completion of 50% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0153 On completion of 60% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0154 On completion of 70% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0155 On completion of 80% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0156 On completion of 90% for the total length of trench excavation	0	03-Mar-14 A			100%									
TG-CC-C2-M-0157 On completion of 100% for the total length of trench excavation	0	20-Mar-14*	16-Jul-13	-246	0%									
TG-CC-C2-M-0158 On completion of 10% for the total length of pipelaying and mechanical works	0	08-Dec-12 A			100%							•	♦	
TG-CC-C2-M-0159 On completion of 20% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0160 On completion of 30% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0161 On completion of 40% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0162 On completion of 50% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0163 On completion of 60% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0164 On completion of 70% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0165 On completion of 80% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0166 On completion of 90% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0167 On completion of 100% for the total length of pipelaying and mechanical works	0	03-Mar-14 A			100%									
TG-CC-C2-M-0168 On completion of 10% for the total length of permanent reinstatement	0	10-Dec-12 A			100%							•	<u>ہ</u>	
TG-CC-C2-M-0169 On completion of 20% for the total length of permanent reinstatement	0	03-Mar-14 A			100%									
TG-CC-C2-M-0170 On completion of 30% for the total length of permanent reinstatement	0	03-Mar-14 A			100%									
TG-CC-C2-M-0171 On completion of 40% for the total length of permanent reinstatement	0	03-Mar-14 A			100%									
TG-CC-C2-M-0172 On completion of 50% for the total length of permanent reinstatement	0	03-Mar-14 A			100%									
TG-CC-C2-M-0173 On completion of 60% for the total length of permanent reinstatement	0	03-Mar-14 A			100%									
TG-CC-C2-M-0174 On completion of 70% for the total length of permanent reinstatement	0	03-Mar-14 A			100%									
TG-CC-C2-M-0175 On completion of 80% for the total length of permanent reinstatement	0	03-Mar-14 A			100%									
					·					_				
Remaining Level of Effort Actual Work Critical Remaining Work	Milestone									Page 3 d	of 6			

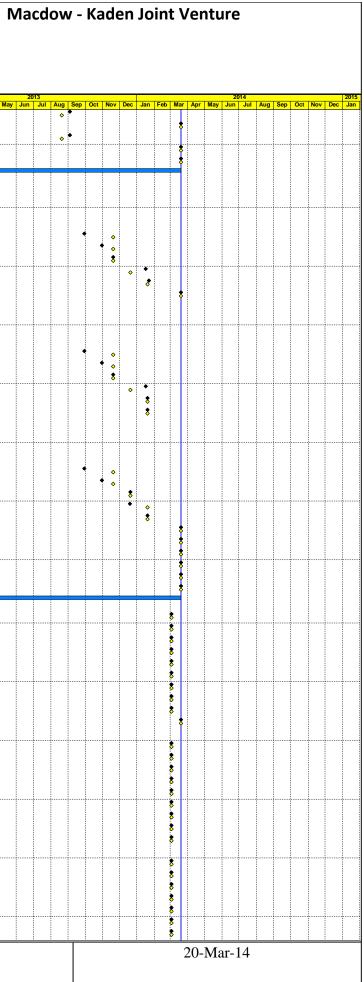


Installation of Submarine Gas Pipelines and Associated Facilities From To Kwa Wan to North Point for Former Kai Tak Airport Development

UPDATED MASTER PROGRAMME REV. 27

Progress Report as of 20 March 2014

	Duration						c Jan Fel	b Mar	Apr May	/ Jun Jul	Aug Se	ep Oct N	lov Dec	Jan Feb	Mar Apr	r May Ji
TG-CC-C2-M-0176 On completion of 90% for the total length of permanent reinstatement	0	03-Mar-14 A				100%										
TG-CC-C2-M-0177 On completion of 100% for the total length of permanent reinstatement	0	03-Mar-14 A				100%										
TG-CC-C2-M-0178 On completion of all cathodic protection works	0	03-Mar-14 A				100%										
TG-CC-C2-M-0179 On completion of final air testing to the satisfaction of the Engineer	0	03-Mar-14 A				100%										
TG-CC-C2-M-0180 On completion of hydrostatic testing to the satisfaction of the Engineer	0	03-Mar-14 A				100%										
TG-CC-C2-M-0181 On completion of vacuum drying to the satisfaction of the Engineer	0	03-Mar-14 A				100%										
TG-CC-C2-M-0182 On completion of the whole of the works under this Cost Centre to the satisfaction of the Engineer	0	03-Mar-14 A				100%										
t Centre D	0 06-Mar-14 A	06-Mar-14 A				0%										
TG-CC-D-M-0183 On completion of 10% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0184 On completion of 20% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0185 On completion of 30% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0186 On completion of 40% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0187 On completion of 50% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0188 On completion of 60% for the total length of trench excavation		06-Mar-14 A				100%										
TG-CC-D-M-0189 On completion of 70% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0190 On completion of 80% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0191 On completion of 90% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0192 On completion of 100% for the total length of trench excavation	0	06-Mar-14 A				100%										
TG-CC-D-M-0193 On completion of 10% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0194 On completion of 20% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0195 On completion of 30% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0196 On completion of 40% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0197 On completion of 50% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0198 On completion of 60% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0199 On completion of 70% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0200 On completion of 80% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0201 On completion of 90% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0202 On completion of 100% for the total length of pipelaying and mechanical works	0	06-Mar-14 A				100%										
TG-CC-D-M-0203 On completion of 10% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0204 On completion of 20% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0205 On completion of 30% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0206 On completion of 40% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0207 On completion of 50% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0208 On completion of 60% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0209 On completion of 70% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0210 On completion of 80% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0211 On completion of 90% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0212 On completion of 100% for the total length of permanent reinstatement	0	06-Mar-14 A				100%										
TG-CC-D-M-0213 On completion of all cathodic protection works	0	06-Mar-14 A				100%										
TG-CC-D-M-0214 On completion of final air testing to the satisfaction of the Engineer	0	06-Mar-14 A				100%										
TG-CC-D-M-0215 On completion of hydrostatic testing to the satisfaction of the Engineer	0	06-Mar-14 A				100%										
TG-CC-D-M-0216 On completion of vacuum drying to the satisfaction of the Engineer	0	06-Mar-14 A				100%										
TG-CC-D-M-0218 On completion of the whole of the works under this Cost Centre to the satisfaction of the Engineer	0	06-Mar-14 A	00 1 10	10 1 10		100%										
t Centre F	0 20-Mar-14	20-Mar-14	02-Jan-13	19-Jun-13	-273	0%										
TG-CC-F-M-0219 Down payment on conclusion of contract	0	20-Mar-14*		02-Jan-13	-441	0%										
TG-CC-F-M-0220 Commencement on site	0	20-Mar-14*		29-May-13	-294	0%										
TG-CC-F-M-0221 Completion of successful field works (dig verifications not inclusive)	0	20-Mar-14*		05-Jun-13	-287	0%										
TG-CC-F-M-0222 Submission of draft Report	0	20-Mar-14*		12-Jun-13	-280	0%										
TG-CC-F-M-0223 Presentation of Final Report	0	20-Mar-14*		19-Jun-13	-273	0%										
struction Works	1046 04-Jan-12 A	20-Oct-14	30-Jan-13	20-Oct-14	0 79	9.44%								_		
	830 04-Jan-12 A	12-Apr-14	20-Mar-14	12-Apr-14	101 07	7.12%								<u> </u>		<u> </u>
t Centre A - Preliminaries			20 Mai-14	12 Apr-14										_		T
TG-CC-A-A-0800 Construct Contractor's Site Office		15-Mar-12 A				100%										
TG-CC-A-A-0900 Accomodation for RE		19-May-12 A				100%										
TG-CC-A-A-1000 Application for Marine Department Notice		18-Jul-12 A				100%										
TG-CC-A-A-1010 Application for Dumping Permit		09-Aug-12 A				100%	-									
TG-CC-A-A-1037 Application of Construction Noise Permit		13-Apr-12 A				100%		-	1							
TG-CC-A-A-1040 Notification to Ferry Company	24 03-Apr-12 A	18-Apr-12 A				100%										
TG-CC-A-A-1041 Aechaeological Survey	24 20-Mar-14	12-Apr-14	20-Mar-14	12-Apr-14	0	0%										
TG-CC-A-A-1045 Application and Approval of Excavation Permit and TTA for Portion C1, C2 and D for Land Gas Pipelines		04-Apr-13 A				100%						-				
t Centre B - Submarine Gas Pipelines and Landfall Works (from CH(TKW)0 to 3176	6.239) 834 18-Feb-12 A	03-Jul-14	30-Jan-13	03-Jul-14	109 8	37.3%					: :			<u> </u>		
mission, Permit Application and Approval	437 18-Feb-12 A	04-Sep-13 A				100%		4	-	+ +		_		<u> </u>	<u></u>	
TG-CC-B-A-0800 Submission of Hydrographic / Geophysical Surveys Method Statement	18 23-Feb-12 A					100%		<u> </u>								
TG-CC-B-A-0802 Approval of Hydrographic / Geophysical Surveys Method Statement	12 20-Mar-12 A					100%								<u> </u>	<u></u>	📥 🕴
TG-CC-B-A-0805 Submission of Dredging Method Statement by DSD, Hyd, MD, HKCG and the Engineer	12 18-Feb-12 A					100%		-	<u> </u>						+	-+
TG-CC-B-A-0807 Approval of Dredging Method Statement by DSD, Hyd, MD, HKCG and the Engineer	12 13-1 60-12 A					100%				<u></u>						
TG-CC-B-A-0800 Approval of Deuging Method Statement by DSD, Hyu, MD, HXCG and the Engineer TG-CC-B-A-0810 Submission of Submarine Pipe Laying Method Statement and associated Temporary Works Design	12 23-May-12 A 18 18-Feb-12 A					100%		<u> </u>		∔ ⊺						
TG-CC-B-A-0815 Approval of Submarine Pipe Laying Method Statement and associated temporary Works Design	12 03-May-12 A					100%									╧╧┷╧╸	╧┷┷╧
TG-CC-B-A-0615 Approval of Submarine Pipe Laying Method Statement and associated remporary works Design TG-CC-B-A-0830 Submission of Backfilling Method Statement	59 20-Oct-12 A					100%			_							-
	39 20-001-12 A	55 iviay*13 A				.0070				<u> </u>						
										_						
Remaining Level of Effort Actual Work Critical Remaining W	ork ♦ ♦ Milestone			1						D~	ige 4 o	f 6				

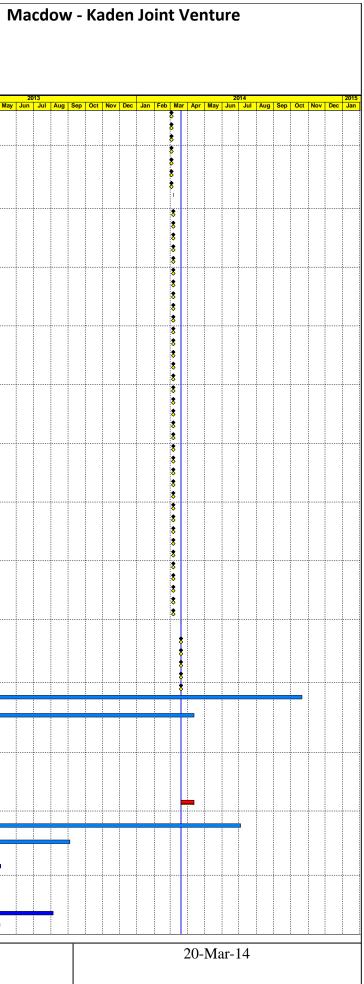


Project Ref. No.: GSPD/SP/TKW-NP/089/2011

Installation of Submarine Gas Pipelines and Associated Facilities From To Kwa Wan to North Point for Former Kai Tak Airport Development

UPDATED MASTER PROGRAMME REV. 27

Progress Report as of 20 March 2014

	Activity Name	Original Early Start Duration	Early Finish	Late Start Late Finish	Float Con	nplete Dec	Jan Feb	Mar Apr	May Jun	Jul Aug S	ep Oct Nov	Dec Jan Feb	Mar Apr M	May 👢
TG-CC-B-A-0	0835 Approval of Backfilling Method Statement	13 04-May-13 A	07-Jun-13 A			100%								-
TG-CC-B-A-0	0840 Submission the Design of Silt Curtain	14 06-Mar-12 A	16-May-12 A			100%	+							
TG-CC-B-A-0	0842 Approval of Silt Curtain Design	11 10-Apr-12 A	11-Jun-12 A			100%								
TG-CC-B-A-0		80 18-Feb-12 A	15-Oct-12 A			100%	-				-			
TG-CC-B-A-0		12 20-Jun-12 A	12-Nov-12 A			100%								
TG-CC-B-A-0		80 18-Feb-12 A	15-Oct-12 A			100%	-							T
TG-CC-B-A-0	0875 Approval of Temporary Work for Seawall at North Point to CEDD and the Engineer	12 19-Jun-12 A	12-Nov-12 A			100%			-	-	+ +			
TG-CC-B-A-0	0900 Submission of Sounding Plan Fronting Seawall to Port Works/CEDD	24 10-Jul-12 A	20-Sep-12 A			100%					•			
TG-CC-B-A-0	0910 Submission of Protection Measure to Existing Facilities	92 18-Feb-12 A	30-Apr-12 A			100%								
TG-CC-B-A-0	0915 Approval of Protection Measure To Existing Facilities	11 02-May-12 A	05-Oct-12 A			100%					-			
TG-CC-B-A-0	0920 Submission of Method Statement for Cathodic Protection	19 09-Nov-12 A	04-Dec-12 A			100%								
TG-CC-B-A-0	0940 Approval of Method Statement for Cathodic Protection	12 05-Nov-12 A	04-Sep-13 A			100%						-		+
TG-CC-B-A-1	1050 Submission of Internal and External Coating Method Statement	15 21-May-12 A	12-Jun-12 A			100%			—					
TG-CC-B-A-1	1085 Approval of Internal and External Coating Method Statement	12 13-Jun-12 A	14-Nov-12 A			100%					 -			
TG-CC-B-A-1	1090 Material Submission for Welding Qualification	15 01-Jun-12 A	18-Jun-12 A			100%								
TG-CC-B-A-1	1095 Approval of Material for Welding Qualification	12 19-Jun-12 A	18-Oct-12 A			100%								
TG-CC-B-A-1	1110 Material Submission of Cathodic Protection (Wire, Electrode, Cable, etc.)	12 05-Nov-12 A	04-Dec-12 A			100%								
TG-CC-B-A-1	1115 Approval of Cathodic Protection (Wire, Electrode, Cable, etc.)	12 05-Dec-12 A	04-Sep-13 A			100%								-
struction Ac		834 03-Mar-12 A		30-Jan-13 03-Jul-14		87.3%								÷
TG-CC-B-A-1		24 23-Mar-12 A				100%		_ <u></u>						
TG-CC-B-A-1		24 16-Mar-12 A	09-Apr-12 A			100%								
TG-CC-B-A-1		12 24-Sep-12 A	10-Oct-12 A			100%					⊢ _			
TG-CC-B-A-1		23 20-Mar-12 A				100%		•						
TG-CC-B-A-1		11 20-Apr-12 A				100%			_					
TG-CC-B-A-1		6 05-Oct-12 A				100%					•_			
TG-CC-B-A-1		2 22-May-12 A				100%							++	
TG-CC-B-A-1		24 03-Mar-12 A	25-Mar-12 A			100%								
TG-CC-B-A-1	-	16 04-Apr-12 A				100%		_						
TG-CC-B-A-1		24 21-Apr-12 A	20-Apr-12 A 20-May-12 A			100%								
TG-CC-B-A-1		194 13-Jun-12 A	03-Jul-14	19-Mar-14 03-Jul-14		45.5%								_
TG-CC-B-A-1 TG-CC-B-A-1		80 13-Jun-12 A	10-Jan-13 A	.5 mai 14 03-Jul-14		45.5% 100%								
TG-CC-B-A-1 TG-CC-B-A-1		3 11-Jan-13 A	10-Jan-13 A 12-Jan-13 A			100%								
TG-CC-B-A-1		6 12-Jan-13 A	24-Jan-13 A			100% 100%						-		
TG-CC-B-A-1		64 19-Oct-12 A	16-Jul-13 A			100% 100%								
TG-CC-B-A-1		64 13-Sep-12 A												
TG-CC-B-A-1		144 02-Apr-12 A	-			100%								
TG-CC-B-A-1		6 29-Sep-12 A	19-Oct-12 A			100%								
TG-CC-B-A-1		58 29-Sep-12 A				100%								
TG-CC-B-A-1		45 14-Mar-13 A				100%								_
TG-CC-B-A-1		20 28-May-13 A				100%							ļļ.	
TG-CC-B-A-1		20 29-Jul-13 A	31-Aug-13 A			100%								
TG-CC-B-A-1		23 10-May-13 A				100%							- -	1
TG-CC-B-A-1		82 26-Jun-13 A	20-Apr-14	30-Mar-13 01-May-13		0.98%								
TG-CC-B-A-1		35 13-Mar-14 A	-	30-Jan-13 04-Mar-13		5.71%								
TG-CC-B-A-1		35 27-Dec-13 A		20-Apr-13 02-May-13		5.71%								
TG-CC-B-A-1		14 05-Nov-13 A	23-Nov-13 A			100%								
TG-CC-B-A-1		14 15-Oct-13 A	23-Nov-13 A			100%								
TG-CC-B-A-1		14 20-Oct-13 A				100%								
TG-CC-B-A-1	· · · · · · · · · · · · · · · · · · ·	64 16-Dec-13 A	19-Dec-13 A			100%								
TG-CC-B-A-1		14 02-Dec-13 A	19-Dec-13 A			100%								
TG-CC-B-A-1	1490 Testing of Cathodic Protection	11 20-Mar-14	30-Mar-14	10-May-13 21-May-13	3 -313	0%								
TG-CC-B-A-1	1500 Carry Out Final IHS to the Backfilled Trench	14 21-Apr-14	04-May-14	07-May-13 21-May-13		0%								
TG-CC-B-A-1	1510 Final Pipelines Testing to the Installed Submarine Gas Pipelines	21 21-Apr-14	11-May-14	01-May-13 22-May-13	3 -354	0%								
TG-CC-B-A-1	1580 Remaining Works and Site Cleaning for Portion D, E and F Handover at North Point	29 05-May-14	02-Jun-14	21-May-13 19-Jun-13	-348	0%								
TG-CC-B-A-1	1600 Remaining Works and Site Cleaning for Portion A1 Handover at To Kwa Wan	12 12-May-14	23-May-14	07-Jun-13 19-Jun-13	-338	0%								
Centre C	1 - Landmains and Associated Works at TKW (from CH(TKW)0 to 0324.147)	741 17-May-12 A		22-Feb-13 15-May-13	3 -380 90	0.28%								
						100%								
	rmit Application and Approval	622 17-May-12 A				100%								
	-0820 Submission of Land Pipe Laying Method Statement and Temporary Works Design	24 17-May-12 A				100%								
	-0840 Approval of Land Pipe Laying Method Statement and Temporary Works Design	12 02-Aug-12 A				100%					-	_		
	-0860 Submission of TTA to TD, HKP, Hyd and other Authorities for Pipe Laying (V.O. 1)	50 17-Jul-12 A	13-Dec-12 A			100%								
	-0880 Approval of TTA by TD, HKP, Hyd and other Authorities for Pipe Laying(V.O. 1)	25 14-Dec-12 A				100%								
TG-CC-C1-A-	-0900 Application to RMO for TTA at Section C1 Land Gas Pipelines(V.O. 1)	12 20-Jan-14 A				100%								
struction Ac	ctivities	506 06-Oct-12 A	30-May-14	22-Feb-13 15-May-13	3 -380 85	5.77%								7
TG-CC-C1-A-	-0950 Implementation of TTA	3 09-Sep-13 A	09-Sep-13 A			100%								
TG-CC-C1-A-	-1000 Mobilization of Plant and Equipment	3 06-Oct-12 A	09-Oct-12 A			100%					•	-		
TG-CC-C1-A-	-1005 Excavate Land Mains at Car Park (CH(TKWLL).0 - 324.147)	156 09-Oct-12 A	11-Jan-14 A			100%								-
TG-CC-C1-A-	-1015 Lay Land Mains at Car Park (CH(TKWLL)0 - 324.147)	161 07-Nov-12 A	29-Mar-14	22-Feb-13 04-Mar-13	-390 93	3.78%								
TG-CC-C1-A-	-1025 Backfill Land Mains at Car Park (CH(TKWLL)0 - 324.147)	160 10-Nov-12 A	05-Apr-14	22-Feb-13 11-Mar-13	-390 89	9.38%								-
TG-CC-C1-A-	-1115 Install Cathodic Protection	13 03-Mar-14 A	18-Apr-14	14-Mar-13 27-Mar-13	-387	0%								
	-1125 Final Air Testing	7 06-Apr-14	12-Apr-14	12-Mar-13 19-Mar-13		0%								
				I		Li		1		Daris E	40			<u> </u>
	ing Level of Effort Actual Work Critical Remaining Work			1					F	Page 5 d	nrhi			

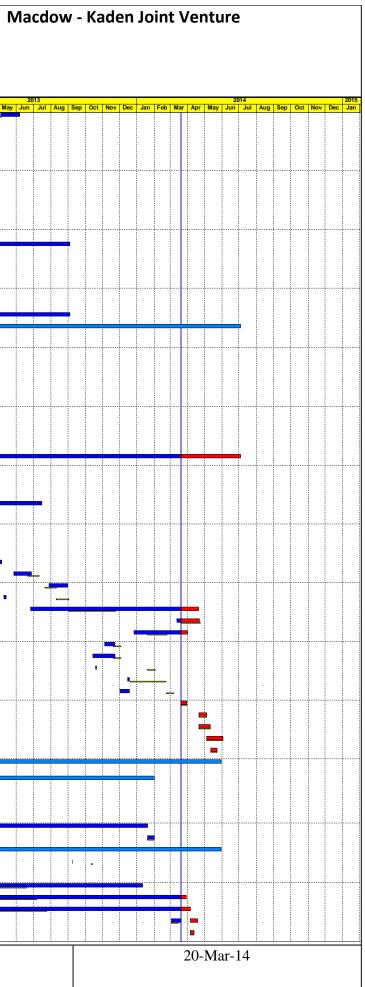


Project Ref. No.: GSPD/SP/TKW-NP/089/2011

Installation of Submarine Gas Pipelines and Associated Facilities From To Kwa Wan to North Point for Former Kai Tak Airport Development

UPDATED MASTER PROGRAMME REV. 27


Progress Report as of 20 March 2014


TC-CC-C1-A-1125 Hydrostatic Testing	Duration 7 13-Apr-14	10-Apr 14	20 Mc- 40	27 Mc- 40				in Iniai	Apr M	ay Jun	Jul Aug S	ep Oct No	Dec Jan	Feb Mar Ap	r May Jun
TG-CC-C1-A-1135 Hydrostatic Testing TG-CC-C1-A-1260 Vacuum Drying	7 13-Apr-14 8 20-Apr-14	19-Apr-14 27-Apr-14	20-Mar-13 28-Mar-13			0% 0%									
TG-CC-C1-A-1200 Vacuum Drying	33 28-Apr-14	30-May-14		15-May-13		0%									
Centre C2 - Landmains and Associated Works at TKW (from CH(TKWLL)324.147 to 1152)	926 01-Mar-12 A		12749110	io may io		100%									
mission, Permit Application and Approval	519 01-Mar-12 A					100%									
TG-CC-C2-A-0500 Submission of Land Pipe Laving Method Statement and Temporary Works Design	26 17-May-12 A					100%									
TG-CC-C2-A-0550 Approval of Land Pipe Laying Method Statement and Temporary Works Design	12 02-Aug-12 A	-				100%					- i L	_			
TG-CC-C2-A-0580 Submission of TTA to TD, HKP, Hyd and other Authorities for Pipe Laying	25 01-Mar-12 A	-				100%			_	_	_				
TG-CC-C2-A-0620 Approval of TTA by TD, HKP, Hyd and other Authorities for Pipe Laying	24 14-May-12 A	09-Mar-13 A				100%			I	-					
TG-CC-C2-A-0640 Application to RMO for TTA at Section C2 Land Gas Pipelines	11 27-Jul-12 A	09-Mar-13 A				100%					—				
TG-CC-C2-A-3010 Submission of TTA to TD, HKP, Hyd and other Authorities for Pipe Laying (V.O. 2)(CH490-500)(CH880-900)	27 17-Jul-12 A	07-Sep-12 A				100%						-			
TG-CC-C2-A-3020 Approval of TTA by TD, HKP, Hyd and other Authorities for Pipe Laying (V.O. 2)(CH490-500)(CH880-900)	12 07-Sep-12 A	09-Mar-13 A				100%					•				
TG-CC-C2-A-3030 Application to RMO for TTA at Section C2 Land Gas Pipelines (V.O. 2)(CH490-500)(CH880-900)	12 22-Sep-12 A	09-Mar-13 A				100%									
struction Activities	861 01-Jun-12 A					100%									
TG-CC-C2-A-0650 Implementation of 1st TTA at Chi Kiang Street, Yuk Yat Street and Kwei Chau Street	0 01-Jun-12 A					100%									
TG-CC-C2-A-0700 Mobilization of Plant and Equipment at Chi Kiang Street	0 03-Mar-14 A					100%									
TG-CC-C2-A-0720 Excavate land mains at Chi Kiang Street (CH(TKWLL)324.147 - 400)	0 03-Mar-14 A					100%									
TG-CC-C2-A-0730 Lay land mains at Chi Kiang Street (CH(TKWLL)324.147 - 400)	0 16-Mar-14 A					100%									
TG-CC-C2-A-0740 Backfill land mains at Chi Kiang Street (CH(TKWLL)324.147 - 400)	0 03-Mar-14 A					100%									
TG-CC-C2-A-0800 Mobilization of Plant and Equipment at Yuk Yat Street TG-CC-C2-A-0810 Excavate land mains at Yuk Yat Street (CH(TKWLL)400 - 700)	0 05-Jun-12 A 0 06-Jul-12 A					100% 100%									
TG-CC-C2-A-0810 Excavate land mains at Yuk Yat Street (CH(TKWLL)400 - 700) TG-CC-C2-A-0820 Lay land mains at Yuk Yat Street (CH(TKWLL)400 - 700)	0 06-Jul-12 A 0 09-Jul-12 A	03-Mar-14 A 03-Mar-14 A				100%									
TG-CC-C2-A-0020 Layland mains at fuk fat Street (CH(TKWLL)400 - 700) TG-CC-C2-A-0830 Backfill land mains at Yuk Yat Street (CH(TKWLL)400 - 700)	0 09-Jul-12 A 0 11-Jul-12 A	03-Mar-14 A				100%									
TG-CC-C2-A-0050 Backhin and Hains at Tuk Fat Sueet (CFI(TKWEL)400 - 700) TG-CC-C2-A-1025 Mobilization of Plant and Equipment at Kwei Chau Street	0 03-Mar-14 A					100%									
TG-CC-C2-A-1030 Excavate land mains at Kwei Chau Street (CH(TKWLL)700 - 850)	0 03-Mar-14 A					100%									
TG-CC-C2-A-1040 Lay land mains at Kwei Chau Street (CH(TKWLL)700 - 850)	0 03-Mar-14 A					100%									
TG-CC-C2-A-1050 Backfill land mains at Kwei Chau Street (CH(TKWLL)700 - 850)	0 03-Mar-14 A	03-Mar-14 A				100%									
TG-CC-C2-A-1480 Mobilization of Plant and Equipment at Wai King Street	0 03-Mar-14 A	03-Mar-14 A				100%									
TG-CC-C2-A-1500 Excavate land mains at Wai King Street (CH(TKWLL) 850 - 990)	0 03-Mar-14 A	03-Mar-14 A				100%									
TG-CC-C2-A-1510 Lay land mains at Wai King Street (CH(TKWLL) 850 - 990)	0 03-Mar-14 A	03-Mar-14 A				100%									
TG-CC-C2-A-1520 Backfill land mains at Wai King Street (CH(TKWLL) 850 - 990)	0 03-Mar-14 A	03-Mar-14 A				100%									
TG-CC-C2-A-1980 Mobilization of Plant and Equipment at San Ma Tau Street	0 13-Jun-12 A	14-Jun-12 A				100%				1					
TG-CC-C2-A-2000 Excavate land mains at San Ma Tau Street (CH(TKWLL) 990 - 1152)	0 14-Jun-12 A	03-Mar-14 A				100%				-					
TG-CC-C2-A-2010 Lay land mains at San Ma Tau Street (CH(TKWLL) 990 - 1152)	0 18-Jul-12 A	03-Mar-14 A				100%									
TG-CC-C2-A-2020 Backfill land mains at San Ma Tau Street (CH(TKWLL) 990 - 1152)	0 20-Jul-12 A	03-Mar-14 A				100%									
TG-CC-C2-A-2950 Install Cathodic Protection	0 03-Mar-14 A					100%									
TG-CC-C2-A-2960 Final Air Testing	0 03-Mar-14 A					100%									
TG-CC-C2-A-2970 Hydrostatic Testing	0 03-Mar-14 A					100%									
TG-CC-C2-A-2980 Vacuum Drying	0 03-Mar-14 A					100%									
TG-CC-C2-A-3000 Connection to Existing IPB network	0 03-Mar-14 A 658 17-May-12 A					100%						<u> </u>			
Centre D - Landmains and Associated Works at NP (from CH(NPLL)0 to 15.567)															
mission, Permit Application and Approval	616 17-May-12 A					100%									
TG-CC-D-A-1000 Submission of Land Pipe Laying Method Statement and Temporary Works Design	24 17-May-12 A	-				100%									
TG-CC-D-A-1020 Approval of Land Pipe Laying Method Statement and Temporary Works Design	12 02-Aug-12 A					100%						-			
TG-CC-D-A-1030 Submission of TTA to TD, HKP, Hyd and other Authorities for Pipe Laying TG-CC-D-A-1040 Approval of TTA by TD, HKP. Hyd and other Authorities for Pipe Laying	28 14-Oct-13 A 24 14-Oct-13 A					100% 100%									
TG-CC-D-A-1040 Approval of TTA by TD, HKP, Hyd and other Authorities for Pipe Laying TG-CC-D-A-1800 Application to RMO for TTA at the Footpath of Hoi Yu Street	12 25-Oct-13 A					100%									
struction Activities	42 05-Nov-13 A					100%									
TG-CC-D-A-3010 Implementation of TTA	3 05-Nov-13 A					100%									
TG-CC-D-A-3020 Mobilization of Plant and Equipment to Hoi Yu Street	3 07-Nov-13 A					100%									
TG-CC-D-A-3030 Trench Excavation for Land Mains along the Footpath of Hoi Yu Street	0 06-Mar-14 A					100%									
TG-CC-D-A-3040 Lay Land Mains along the Footpath of Hoi Yu Street	0 06-Mar-14 A					100%									
TG-CC-D-A-3050 Backfill Land Mains along the Footpath of Hoi Yu Street	0 06-Mar-14 A					100%									
TG-CC-D-A-3070 Install Cathodic Protection	0 06-Mar-14 A	06-Mar-14 A				100%									
TG-CC-D-A-3080 Final Air Testing	0 06-Mar-14 A	06-Mar-14 A				100%									
TG-CC-D-A-3090 Hydrostatic Testing	0 06-Mar-14 A	06-Mar-14 A				100%									
TG-CC-D-A-3100 Vacuum Drying	0 06-Mar-14 A	06-Mar-14 A				100%									
TG-CC-D-A-3300 Connect to Existing IBP at Hoi Yu Street	0 06-Mar-14 A	06-Mar-14 A				100%									
Centre E - Daywork	215 20-Mar-14	20-Oct-14	20-Mar-14	20-Oct-14	0	0%									
TG-CC-E-A-1000 Daywork	215 20-Mar-14	20-Oct-14	20-Mar-14	20-Oct-14	0	0%									
Centre F - Intelligent Pigging Inspection	380 12-Mar-13 A	03-Jun-14	20-May-13	19-Jun-13	-349	80%									
	380 12-Mar-13 A			19-Jun-13		80%									
mission, Permit Application and Approval TG-CC-F-A-0500 Submission of Intelligent Pigging Inspection Method Statement	72 12-Mar-13 A		20-1/1ay-13	13-341-13	-349	100%									
TG-CC-F-A-0500 Submission of Intelligent Pigging Inspection Method Statement TG-CC-F-A-0510 Approval of Intelligent Pigging Inspection Method Statement	72 12-Mar-13 A 24 20-Mar-13 A		20-Mav-13	22-May-13	-303	100% 91.67%									
TG-CC-F-A-1020 Submission of Draft Report of Intelligent Pigging Inspection	6 19-May-14	21-Mar-14 24-May-14	20-iviay-13 03-Jun-13			91.67% 0%									
TG-CC-F-A-1020 Submission of Final Report of Intelligent Pigging Inspection TG-CC-F-A-1040 Submission of Final Report of Intelligent Pigging Inspection	10 25-May-14	24-iviay-14 03-Jun-14		19-Jun-13		0%									
struction Activities	7 12-May-14	18-May-14		29-May-13		0%									
TG-CC-F-A-1100 Carry Out Intelligent Pigging Inspection	7 12-May-14		22-May-13			0%									
	way 14			ay 10	007	570	: 1						<u> </u>		_ : _ i

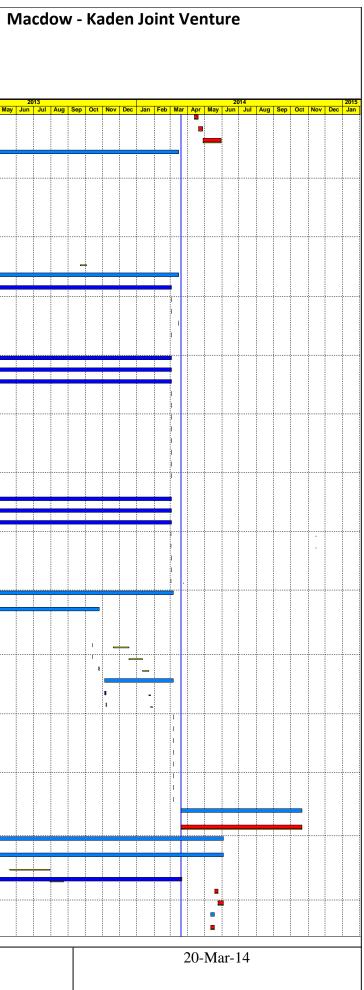



Annex D


Marine Water Quality Monitoring

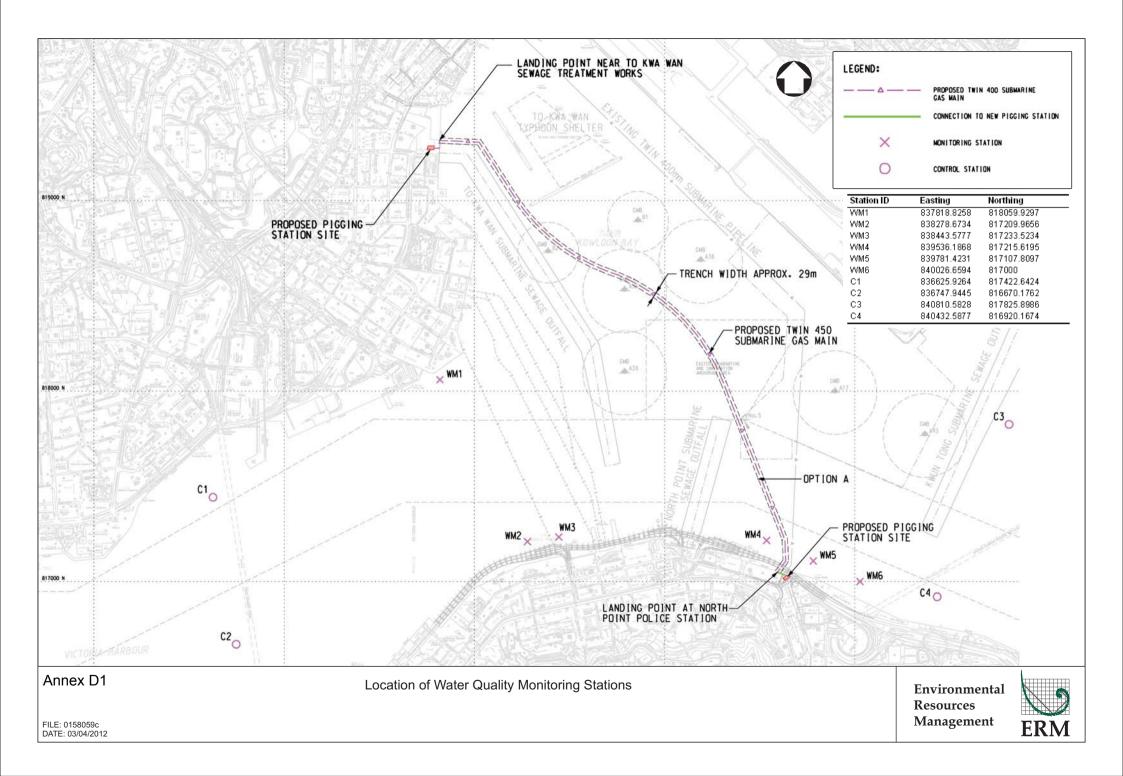


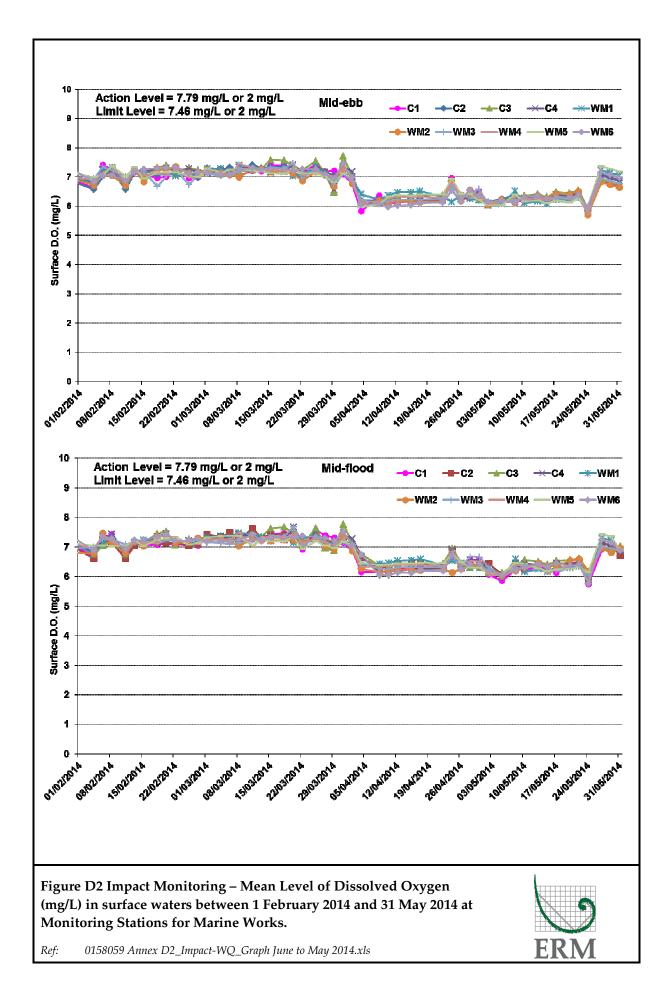

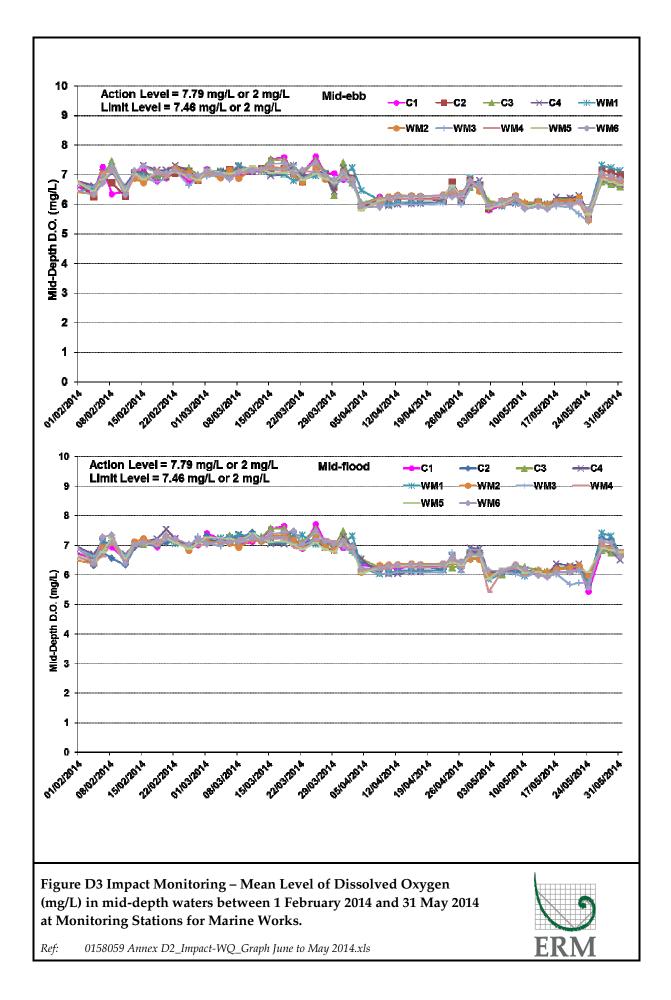

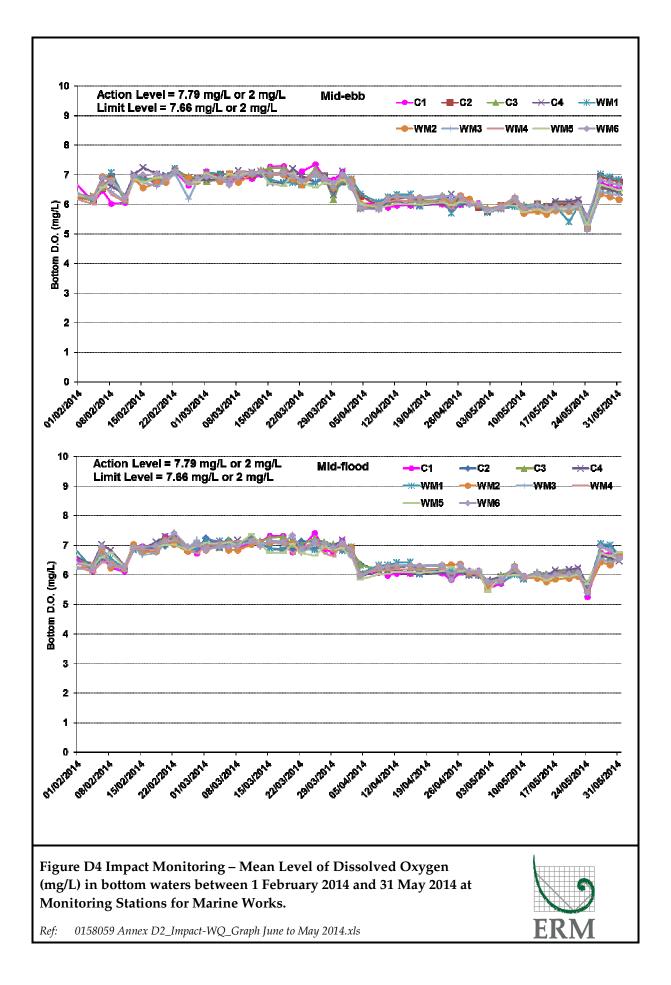


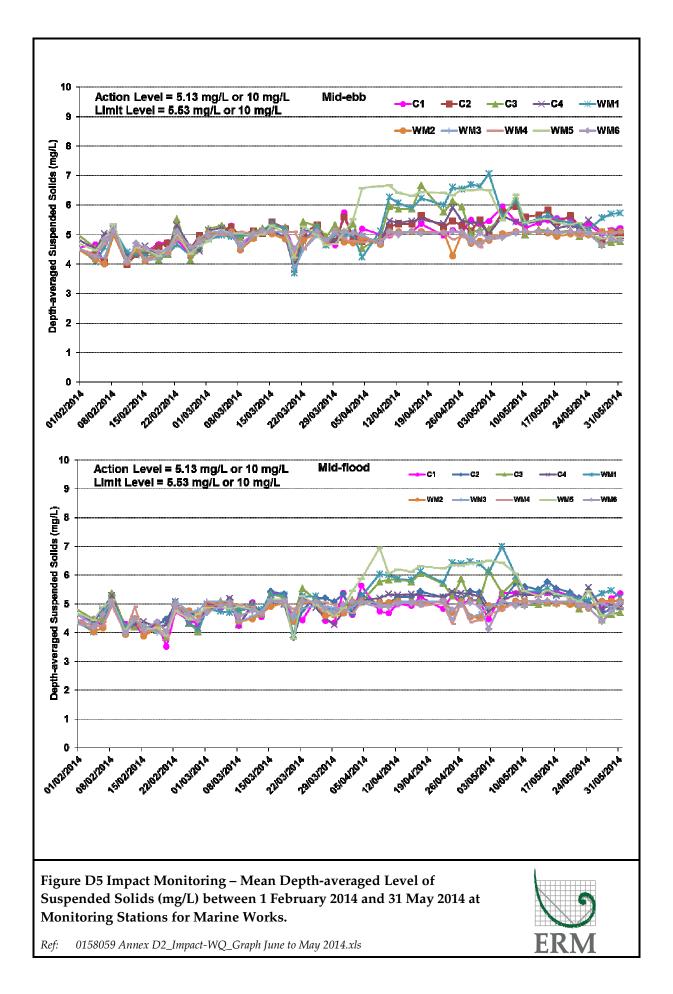


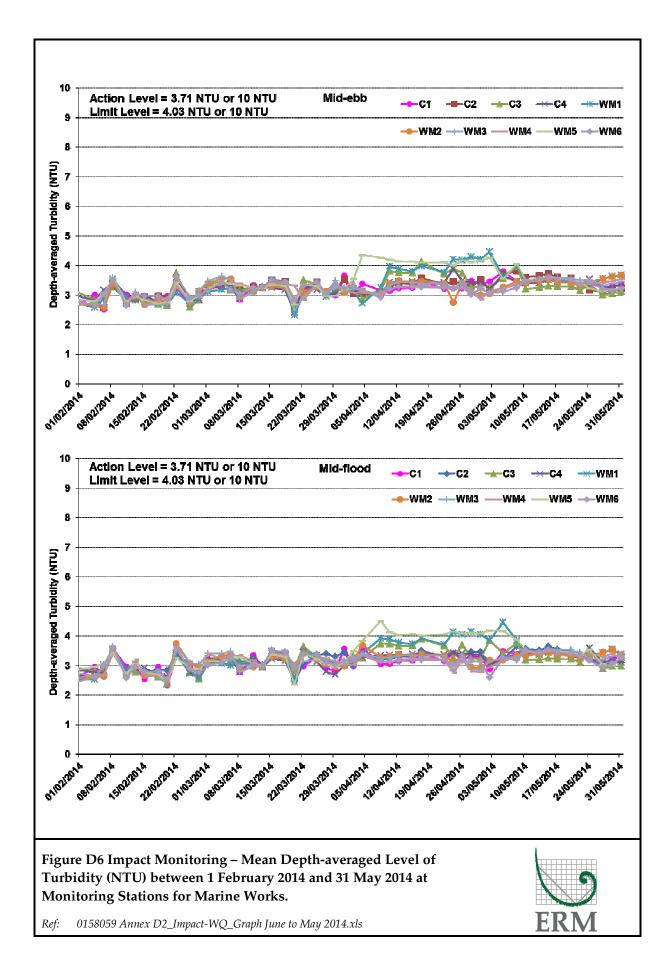

Annex E

Air Borne Noise Monitoring

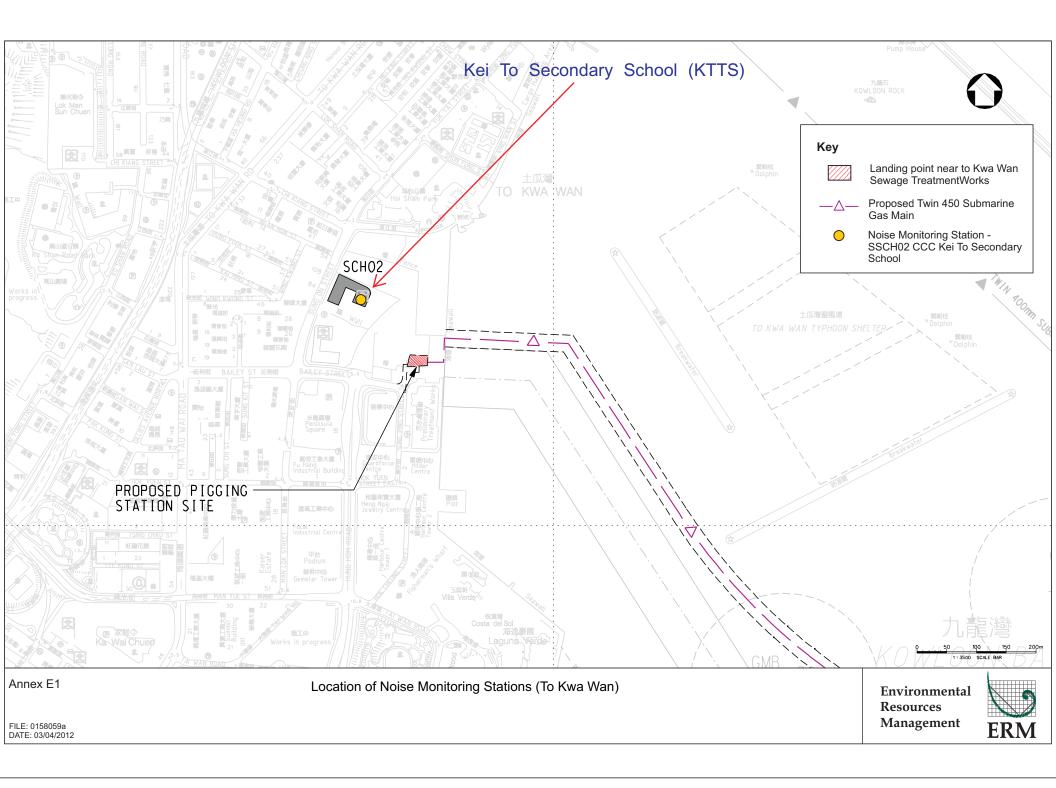

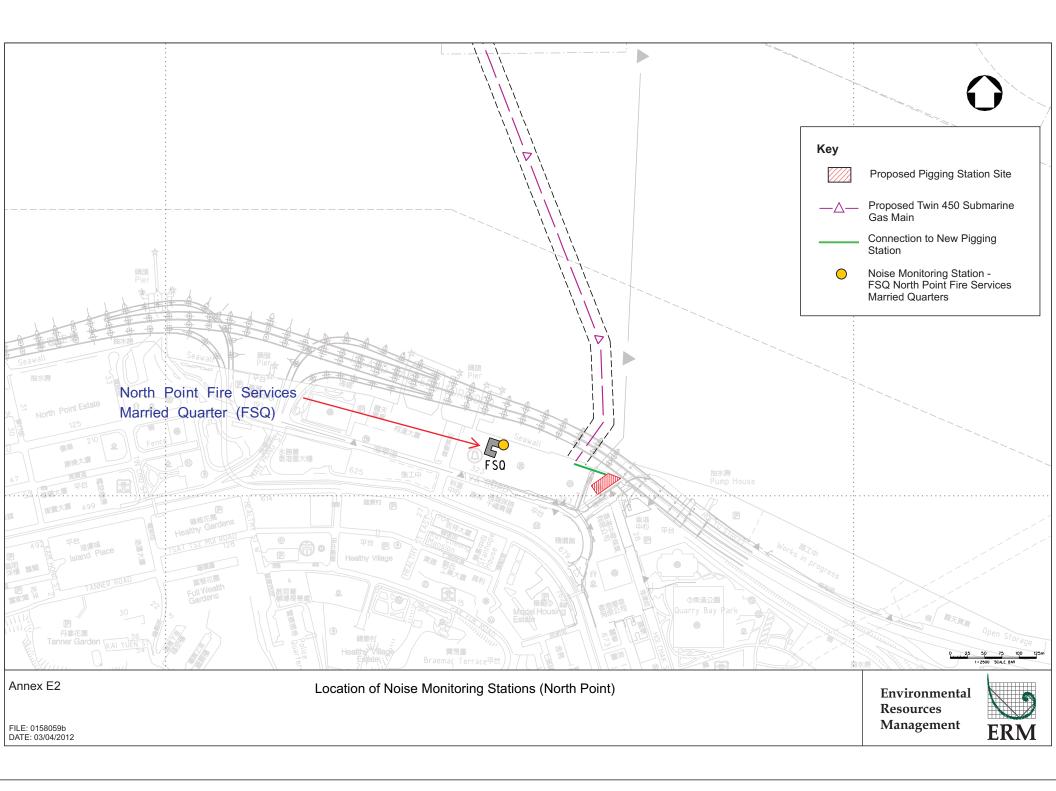

Annex E3 Noise Monitoring Results

Daytime Noise Monitoring Results

FSQ Monitoring Station

				Noise	level (dB(A)), 30 min	Major Construction	Other Noise			Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Noise Source(s) Observed	Source(s) Observed	Remarks	Temp. (°C)	(m/s)	Model / ID	Model / ID
07-Feb-14	11:20	11:50	Fine	72	73	70	-	Traffic noise	-	20	0.6	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
12-Feb-14	14:12	14:42	Cloudy	73	75	71	-	Traffic noise	-	8	0.6	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
19-Feb-14	11:00	11:30	Sunny	72	74	70	-	Traffic noise	-	9	0.6	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
			Min.	72									•
			Max.	73									

SCH02 Monitoring Station

				Noise	level (dB(A)), 30 min	Major Construction	Other Noise			Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Noise Source(s) Observed	Source(s) Observed	Remarks	Temp. (°C)	(m/s)	Model / ID	Model / ID
06-Feb-14	09:00	09:30	Cloudy	62	64	60	-	Traffic noise	-	18	0.8	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
13-Feb-14	09:00	09:30	Cloudy	62	64	60	-	Traffic noise	-	8	0.8	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
20-Feb-14	13:00	13:30	Sunny	62	64	60	-	Traffic noise	-	15	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
27-Feb-14	13:00	13:30	Fine	63	65	61	-	Traffic noise	-	20	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
			Min.	62									
			Max.	63									

Annex E4 Noise Monitoring Results

Daytime Noise Monitoring Results

FSQ Monitoring Station

				Noise	level (dB(A)), 30 min	Major Construction	Other Noise			Wind	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Noise Source(s) Observed	Source(s) Observed	Remarks	Temp. (℃)	Speed (m/s)	Model / ID	Model / ID
01-Mar-14	11:00	11:30	Cloudy	72	74	70	-	Traffic noise	-	20	0.4	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
07-Mar-14	10:23	10:53	Cloudy	72	73	70	-	Traffic noise	-	15	0.5	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
15-Mar-14	11:15	11:45	Cloudy	71	72	69	-	Traffic noise	-	17	0.5	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
19-Mar-14	09:12	09:42	Cloudy	71	72	70	-	Traffic noise	-	23	0.6	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
26-Mar-14	09:08	09:38	Cloudy	73	74	71	-	Traffic noise	-	23	0.8	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
	•		Min. Max.	71 73		•	•						

SCH02 Monitoring Station

				Noise I	evel (dB(A)), 30 min	Major Construction	Other Noise	_		Wind	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Noise Source(s) Observed	Source(s) Observed	Remarks	Temp. (℃)	Speed (m/s)	Model / ID	Model / ID
06-Mar-14	13:00	13:30	Cloudy	62	65	60	-	Traffic noise	-	15	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
13-Mar-14	13:00	13:30	Cloudy	62	64	60	-	Traffic noise	-	17	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
20-Mar-14	09:00	09:30	Fine	62	64	60	-	Traffic noise	-	21	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
27-Mar-14	09:00	09:30	Cloudy	63	65	61	-	Traffic noise	-	24	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
			Min. Max.	62 63						·			

Remark: (1) School examinations are carried out in CCC Kei To Secondary School every Wednesday from 19 March 2014 to 14 May 2013 and on 7 April 2014 and 5 & 12 May 2014.

Annex E5 Noise Monitoring Results

Daytime Noise Monitoring Results

FSQ Monitoring Station

				Noise	level (dB(A)), 30 min	Major Construction	Other Noise			Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Noise Source(s) Observed	Source(s) Observed	Remarks	Temp. (°C)	(m/s)	Model / ID	Model / ID
04-Apr-14	14:08	14:38	Cloudy	74	75	72	-	Traffic noise	-	20	0.9	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
09-Apr-14	14:20	14:50	Sunny	73	74	70	-	Traffic noise	-	24	0.5	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
15-Apr-14	13:58	14:28	Fine	73	74	71	-	Traffic noise	-	22	0.6	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
24-Apr-14	08:38	09:08	Cloudy	73	74	72	-	Traffic noise	-	21	0.7	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
29-Apr-14	16:41	17:11	Fine	72	74	70	-	Traffic noise	-	23	0.3	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
			Min. Max.	72 74							•		

SCH02 Monitoring Station

_		_		Noise	level (dB(A)), 30 min	Major Construction	Other Noise	_		Wind Speed	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Noise Source(s) Observed	Source(s) Observed	Remarks	Temp. (°C)	(m/s)	Model / ID	Model / ID
03-Apr-14	09:00	09:30	Cloudy	63	65	61	-	Traffic noise	-	19	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
10-Apr-14	13:00	13:30	Cloudy	62	65	60	-	Traffic noise	-	22	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
17-Apr-14	13:00	13:30	Sunny	62	64	60	-	Traffic noise	-	24	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
24-Apr-14	09:00	09:30	Cloudy	62	64	60	-	Traffic noise	-	21	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
30-Apr-14	09:00	09:30	Fine	62	65	60	-	Traffic noise	-	23	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
			Min. Max.	62 63									

Remark: (1) School examinations are carried out in CCC Kei To Secondary School every Wednesday from 19 March 2014 to 14 May 2013 and on 7 April 2014 and 5 & 12 May 2014.

Annex E6 Noise Monitoring Results

Daytime Noise Monitoring Results


FSQ Monitoring Station


_				Noise	level (dB(A)), 30 min	Major Construction	Other Noise		_	Wind Speed (m/s)	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Noise Source(s) Observed	Source(s) Observed	Remarks	Temp. (°C)	(m/s)	Model / ID	Model / ID
09-May-14	09:19	09:49	Cloudy	73	75	72	-	Traffic noise	-	22	1.1	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
14-May-14	10:30	11:00	Cloudy	73	74	71	-	Traffic noise	-	28	0.9	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
23-May-14	08:54	09:24	Cloudy	73	74	71	-	Traffic noise	-	27	0.5	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
28-May-14	15:26	15:56	Sunny	72	73	69	-	Traffic noise	-	30	0.2	RION- NL31 (S/N 00410224)	RION- NC73 (S/N 10997142)
<u>.</u>			Min.	72									<u>_</u>
			Max.	73									

SCH02 Monitoring Station

_	_			Noise	level (dB(A)), 30 min	Major Construction	Other Noise		_	Wind Speed (m/s)	Noise Meter	Calibrator
Date	Start Time	End Time	Weather	Leq	L10	L90	Noise Source(s) Observed	Source(s) Observed	Remarks	Temp. (°C)	(m/s)	Model / ID	Model / ID
08-May-14	09:00	09:30	Cloudy	62	64	60	-	Traffic noise	-	22	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
15-May-14	09:00	09:30	Fine	63	65	61	-	Traffic noise	-	28	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
22-May-14	09:00	09:30	Cloudy	63	65	61	-	Traffic noise	-	29	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
29-May-14	13:00	13:30	Sunny	62	64	60	-	Traffic noise	-	30	0.5	RION- NL18 (S/N 00360030)	RION- NC73 (S/N 10997142)
			Min.	62									
			Max.	63									

Remark: (1) School examinations are carried out in CCC Kei To Secondary School every Wednesday from 19 March 2014 to 14 May 2013 and on 7 April 2014 and 5 & 12 May 2014.

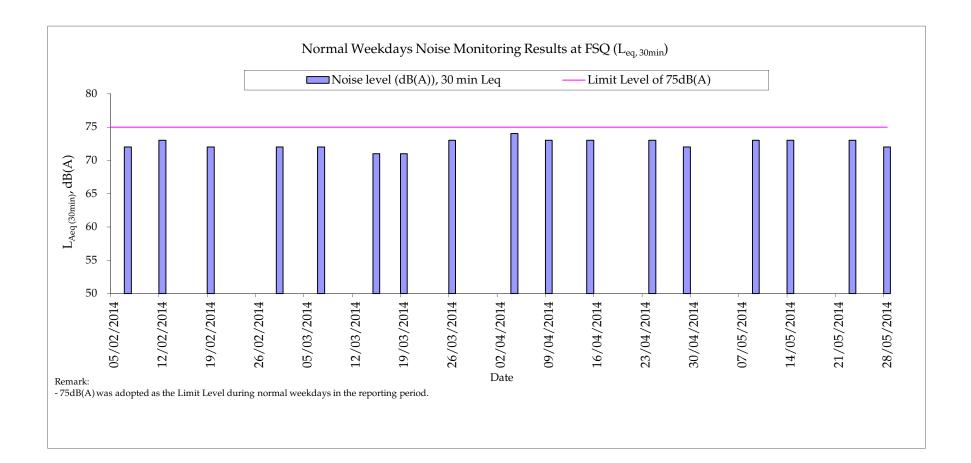

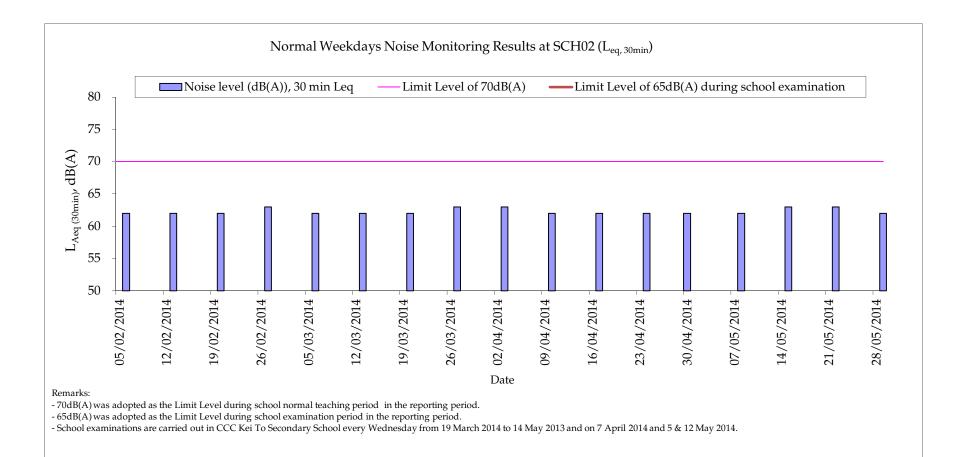

Annex F

Event / Action Plans for Marine Water Quality and Air Borne Noise Monitoring

	Action					
Event	ET ⁽¹⁾	IEC ⁽¹⁾	ER ⁽¹⁾	Contractor(s)		
Action Level Exceedance by one sampling day	1. Repeat <i>in situ</i> measurement to confirm findings;	1. Discuss with ET and Contractor on the mitigations measures;	1. Discuss with IEC on the proposed mitigation measures; and	1. Inform the ER and confirm notification of the non- compliance in writing;		
	2. Identify source(s) of impact;	 Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 	2. Make agreement on the mitigation measures to be implemented	2. Rectify unacceptable practice;		
	3. Inform IEC and Contractor	3. Assess the effectiveness of the implemented mitigation measures		3. Check all plant and equipment		
	 Check monitoring data, all plant, equipment and Contractor's working methods; 	1 0		4. Consider changes of working methods;		
	5. Discuss mitigation measure with IEC and Contractor; and			5. Discuss with ET and IEC and propose mitigation measures to IEC and ER; and		
	6. Repeat measurement on next day of exceedance			6. Implement the agreed mitigation measures.		
Exceedance for two or more consecutive sampling days	1. Repeat in-situ measurement to confirm finding;	1. Discuss with ET and Contractor on the mitigation measures;	1. Discuss with IEC on the proposed mitigation measures;	1. Inform the Engineer and confirm notification of the non-compliance in writing;		
	2. Identify source(s) of impact;	 Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 	2. Make agreement on mitigation measures to be implemented; and	2. Rectify unacceptable practice;		
	3. Inform IEC and Contractor;	3. Assess the effectiveness of the implemented mitigation measures	3. Assess the effectiveness of the implemented mitigation measures	3. Check all plant and equipment		
	4. Check monitoring data, all plant, equipment and Contractor's working methods;			4. Consider changes of working methods;		
	5. Discuss mitigation measure with IEC and Contractor;			5. Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; and		

Event and Action Plan for Water Quality Monitoring during Construction Phase

Annex F1

	Action					
Event	ET ⁽¹⁾	IEC ⁽¹⁾	ER (1)	Contractor(s)		
	6. Ensure mitigation measures are implemented			6. Implement the agreed mitigation measures.		
	7. Prepare to increase the monitoring frequency to daily; and					
	8. Repeat measurement on next day of exceedance.					
Limit Level						
Exceedance by one sampling day	1. Repeat <i>in situ</i> measurement to confirm findings;	1. Discuss with ET and Contractor on the mitigations measures;	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures;	 Inform the Engineer and confirm notification of the non- compliance in writing; 		
	2. Identify source(s) of impact;	 Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 	2. Request Contractor to critically review the working methods	2. Rectify unacceptable practice;		
	3. Inform IEC and Contractor and EPD	3. Assess the effectiveness of the implemented mitigation measures	Make agreement on mitigation measures to be implemented; and	3. Check all plant and equipment		
	 Check monitoring data, all plant, equipment and Contractor's working methods; 	1 0	4. Assess the effectiveness of the implemented mitigation measures	 Consider changes of working methods; 		
	5. Discuss mitigation measure with IEC and Contractor;			5. Discuss with ET and IEC and ER and propose mitigation measures to IEC and ER within 3 working days; and		
	6. Repeat measurement on next day of exceedance			6. Implement the agreed mitigation measures.		
	7. Increase the monitoring frequency to daily until no exceedance of Limit Level					
Exceedance two or more consecutive sampling days	1. Repeat <i>in situ</i> measurement to confirm findings;	1. Discuss with ET and Contractor on the mitigations measures;	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures;	 Inform the ER and confirm notification of the non- compliance in writing; 		
	2. Identify source(s) of impact;	 Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; and 	2. Request Contractor to critically review the working methods	2. Rectify unacceptable practice;		

		Acti	ion	
Event	ET (1)	IEC ⁽¹⁾	ER ⁽¹⁾	Contractor(s)
	3. Inform IEC and Contractor and EPD	3. Assess the effectiveness of the implemented mitigation measures	 Make agreement on mitigation measures to be implemented; 	3. Check all plant and equipment
	4. Check monitoring data, all plant, equipment and Contractor's working methods;		4. Assess the effectiveness of the implemented mitigation measures; and	4. Consider changes of working methods;
	5. Discuss mitigation measure with IEC, ER and Contractor;		5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit Level	5. Discuss with ET and IEC and ER and propose mitigation measures to IEC and ER within 3 working days;
	6. Ensure mitigation measures are implemented; and			6. Implement the agreed mitigation measures; and
	7. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days			7. As directed by the Engineer, to slow down or to stop all to part of the marine work or construction activities.

Note:

(1) ET – Environmental Team, IEC – Independent Environmental Checker, ER – Engineer's Representative

	Action					
Event	ET (1)	IEC ⁽¹⁾	ER ⁽¹⁾	Contractor(s)		
Action Level	1. Notify IEC and the Contractor	1. Review with analysed results submitted by ET	1. Confirm receipt of notification of exceedance in writing	1. Submit noise mitigation proposals to IEC		
	2. Carry Out investigation	2. Review the proposed remedial measures by the Contractor and advise ER accordingly	2. Notify the Contractor.	2. Implement noise mitigation proposals.		
	3. Report the results of investigation to IEC and the Contractor	3. supervise the implement of remedial measures.	3. Require the Contractor to proposed remedial measures for the analysed noise problem			
	4. Discuss with the Contractor and formulate remedial measures		4. Ensure remedial measures are properly implemented			
	5. Increase monitoring frequency to check mitigation measures					
Limit Level	1. Identify the source	1. Discuss amongst ER, ET Leader and the Contractor on the potential remedial actions	1. Confirm receipt of notification of exceedance in writing	1. Take immediate action to avoid further exceedance		
	2. Notify IEC, ER, EPD and the Contractor	2. Review the Contractor's remedial actions whenever necessary to assure their effectiveness and advise ER accordingly	2. Notify the Contractor	2. Submit proposals for remedial actions to IEC within 3 working days of notification.		
	3. Repeat measurement to confirm findings	3. Supervise the implement of remedial measures.	3. Require the Contractor to proposed remedial measures for the analysed noise problem	3. Implemet the agreed proposals.		
	4. Increase monitoring frequency		4. Ensure remedial measures are properly implemented	4. Resubmit proposals if problem still not under control.		
	5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented		5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated	5. Stop the relevant activity of works as determined by the ER until exceedance is abated.		
	6. Inform IEC, ER and EPD the causes and actions taken for the exceedances					

Annex F2 Event and Action Plan for Air-borne Noise Monitoring during Construction Phase

			Action	
Event	ET ⁽¹⁾	IEC ⁽¹⁾	ER ⁽¹⁾	Contractor(s)
	7. Assess effectiveness of the Contractor's remedial actions and keep IEC, EPD and ER informed the results			
	8. If exceedance stops, cease additional monitoring			
Note:	(1) ET – Environmental Team, IEC – I	ndependent Environmental Cł	ecker, ER – Engineer's Representative	

Annex G

Implementation Schedule

ANNEX G SUMMARY OF MITIGATION MEASURE IMPLEMENTATION SCHEDULE

Environmental Protection Measures	Location	Timing	Status
Water Quality			
<u>Mitigation Measures for Dredging</u> Although adverse water quality impact is not predicted during the construction phase, implementation of the following mitigation measures is recommended to minimise the potential SS impact from dredging activities:	Construction Work Sites (Along the alignment of dredging)	During Marine Dredging works	N.A.
• Dredging shall be carried out by closed grab dredger to minimize release of sediment and other contaminants during dredging;			
• The maximum production rate for dredging from the seabed for installation of the submarine gas pipelines shall not be more than 4,000m ³ per day (and no more than 1 closed grab dredger); and			
• Deployment of frame type silt curtain to fully enclose the grab while dredging works are in progress. An illustration of a typical configuration of frame type silt curtain is shown in EM&A manual Figure 3.10.			
The frame type silt curtain shall be designed to enclose local pollution caused by the grab dredger and suspended by a steel frame mounted on the grab dredger and floating on water. This frame type silt curtain shall be fabricated from permeable, durable, abrasion resistant membrane like geotextiles and be mounted on a floating boom structure. The frame type silt curtain shall also extend to the seabed to cover the entire water column. Steel chain or ballast shall be attached to the bottom of the silt curtain. Mid-ballast may be added as necessary. The structure of the silt curtain shall be maintained by metal grids. The frame type silt curtain shall be capable or reducing sediment loss to outside by a factor of 4 (or about 75%).			
<u>Other Good Site Practices for Dredging</u> Other good site practices that shall be undertaken during dredging includes:			
• all vessels shall be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;			
• all barges / dredgers used shall be fitted with tight fitting seals to their bottom openings to prevent leakage of material;			
• construction activities shall not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site or dumping grounds;			
• barges or hopper shall not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation; and			
• before commencement of dredging works, the holder of the Environmental Permit shall submit detailed proposal of the design and arrangement of the frame type silt curtain to EPD for approval.			
Effluent from Hydrostatic/ Commissioning Tests of the Gas Pipeline System	Construction Work	During	N.A.
For hydrostatic testing of gas pipelines, the gas pipelines would be filled with potable water (a nearly incompressible liquid) and	Sites (General)	Hydrostatic	
examined for leaks or permanent changes in shape with a specified test pressure. The test would be carried out at room temperature		Tests	
and dosing of chemicals into the water for testing is not required. Water used for testing shall be reused as far as possible (e.g. water			

Environmental Protection Measures	Location	Timing	Status
spray for dust suppression on site). To ensure compliance with the standards for effluent discharged into the inshore waters or marine waters of Victoria Harbour WCZ as shown in Tables 9a and 9b of the TM-DSS, sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m3 capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and suited to applications where the influent is pumped.			
Surface Runoff, Sewage and Wastewater from Construction Activities	Construction Work	Construction	Δ
Appropriate measures shall be implemented to control runoff and prevent high loads of SS from entering the marine environment. Proper site management is essential to minimize surface runoff and sewage effluents.	Sites (General)	period	
• Construction site runoff shall be prevented or minimised in accordance with the guidelines stipulated in the EPD's Practice Note for Professional Persons, Construction Site Drainage (ProPECC PN 1/94). All discharges from the construction site shall be controlled to comply with the standards for effluents discharged into the Victoria Harbour WCZ under the TM-DSS. Good housekeeping and stormwater best management practices, as detailed below, shall be implemented to ensure all construction runoff complies with WPCO standards and no unacceptable impact on the WSRs as a result of construction of the proposed submarine gas pipelines;			
• Sedimentation tanks with sufficient capacity, constructed from pre-formed individual cells of approximately 6 to 8 m ³ capacities, are recommended as a general mitigation measure which can be used for settling surface runoff prior to disposal. The system capacity shall be flexible and able to handle multiple inputs from a variety of sources and suited to applications where the influent is pumped;			
• Manholes (including newly constructed ones) shall always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris being washed into the storm runoff being directed into foul sewers;			
• All vehicles and plant shall be cleaned before leaving a construction site to ensure no earth, mud, debris and the like is deposited by them on roads. An adequately designed and located wheel washing bay shall be provided at every site exit, and wash-water shall have sand and silt settled out and removed at least on a weekly basis to ensure the continued efficiency of the process. The section of access road leading to, and exiting from, the wheel-wash bay to the public road shall be paved with sufficient backfill toward the wheel-wash bay to prevent vehicle tracking of soil and silty water to public roads and drains;			
• Precautions shall be taken at any time of year when rainstorms are likely. Actions shall be taken when a rainstorm is imminent or forecast. Actions to be taken during or after rainstorms are summarised in Appendix A2 of ProPECC PN 1/94. Particular attention shall be paid to the control of silty surface runoff during storm events, particularly for areas located near steep slopes;			
• Fuel tanks and storage areas shall be provided with locks and be located on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank, to prevent spilled fuel oils from reaching the coastal waters of the Victoria Harbour and Western and Eastern Buffer WCZs;			
 Portable chemical toilets shall be used to handle construction workforce sewage prior to discharge to the existing trunk sewer. Sufficient numbers of portable toilets shall be provided by a licensed contractor to serve the construction workers. The Contractor should also be responsible for waste disposal and maintenance practices. 			
Waste Management		<u> </u>	
<u>Good Site Practices</u> Adverse impacts related to waste management are not expected to arise, provided that good site practices are strictly followed. Recommendations for good site practices during the construction activities include:	Construction Work Sites (General)	Construction period	Δ

Environmental Protection Measures	Location	Timing	Status
 Nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site 			
 Training of site personnel in proper waste management and chemical handling procedures, separation of chemical wastes with appropriate treatment which is mentioned in Section 4.6.5 			
Provision of sufficient waste disposal points and regular collection of waste			
Barges filled with dredged sediment shall be towed away immediately for disposal. In doing so, odour is not anticipated to be an issue to distant sensitive receivers			
Well planned delivery programme for offsite disposal such that adverse impact from transporting sediment material is not anticipated			
Well maintained PME should be operated on site			
Regular cleaning and maintenance of the drainage systems for construction of the landing points			
Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers			
Vaste Reduction Measures Good management and control can prevent the generation of a significant amount of waste. Waste reduction is best achieved at the lanning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste eduction include:	Construction Work Sites (General)	Construction period	Δ
Sort C&D material from demolition and decommissioning of the existing facilities to recover recyclable portions such as metals;			
Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;			
Encourage collection of aluminium cans by providing separate labelled bins to enable this waste to be segregated from other general refuse generated by the work force;			
Proper storage and site practices to minimise the potential for damage or contamination of construction materials; and			
Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.			
<u>&D Material</u> n order to minimise impacts resulting from collection and transportation of C&D material for off-site disposal, the excavated materials hall be reused on-site as backfilling material and for landscaping works as far as practicable. Surplus C&D material generated from xcavation works shall be disposed of at public fill reception facilities for other beneficial uses. Other mitigation requirements are	Construction Work Sites (General)	Construction period	\checkmark

	Location	Timing	Status
A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) shall be proposed; and			
In order to monitor the disposed of CPD metanial and calid suppress at mublic filling facilities and landfills and to control fly timping			
• In order to monitor the disposal of C&D material and solid wastes at public filling facilities and landfills, and to control fly-tipping,			
a trip-ticket system (e.g. ETWB TCW No. 31/2004) shall be included.	Construction Work	Construction	
General Refuse		Construction	Δ
General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material. Preferably an enclosed and covered	Sites (General)	period	
area shall be provided to reduce the occurrence of 'wind blown' light material.		C 1 1	
Chemical Waste	Construction Work	Construction	Δ
Good quality containers compatible with the chemical wastes shall be used, and incompatible chemicals shall be stored separately.	Sites (General)	period	
Appropriate labels shall be securely attached on each chemical waste container indicating the corresponding chemical characteristics			
of the chemical waste, such as explosive, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a			
licensed collector to transport and dispose of the chemical wastes, to either the approved Chemical Waste Treatment Centre, or			
another licensed facility.			
Marine Dredged Sediment	Construction Work	During Marine	• √
During transportation and disposal of the dredged marine sediments, the following measures shall be taken to minimise potential	Sites (Along the	Dredging	
impacts on water quality:	alignment of	works	
	dredging)		
• Bottom opening of barges shall be fitted with tight fitting seals to prevent leakage of material. Excess material shall be cleaned from			
the decks and exposed fittings of barges and dredgers before the vessel is moved;			
Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the EPD; and Barges or hopper barges shall not be filled to a level that would cause the overflow of materials or sediment laden water during loading or			
transportation.			
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of 			
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. 			
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This 	Proposed dredging	Construction	√
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain 	Proposed dredging near To Kwa Wan	Construction period	√
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain shall extend past the dredger in each direction. This curtain shall remain in a suitable position between the dredger and the corals until 	1 0 0		√
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain shall extend past the dredger in each direction. This curtain shall remain in a suitable position between the dredger and the corals until the dredger is 250m from the corals. 	near To Kwa Wan		√
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain shall extend past the dredger in each direction. This curtain shall remain in a suitable position between the dredger and the corals until the dredger is 250m from the corals. 	near To Kwa Wan		√
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain shall extend past the dredger in each direction. This curtain shall remain in a suitable position between the dredger and the corals until 	near To Kwa Wan		√
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain shall extend past the dredger in each direction. This curtain shall remain in a suitable position between the dredger and the corals until the dredger is 250m from the corals. Hazard to Life 	near To Kwa Wan breakwaters	period	
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain shall ethed past the dredger in each direction. This curtain shall remain in a suitable position between the dredger and the corals until the dredger is 250m from the corals. Hazard to Life Proper general traffic management measures. Minimisation of works activity footprint – dredging and backfilling. 	near To Kwa Wan breakwaters Construction Work	period Construction	
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain shall ethed past the dredger in each direction. This curtain shall remain in a suitable position between the dredger and the corals. Hazard to Life Proper general traffic management measures. Minimisation of works activity footprint – dredging and backfilling. Safety provision during dredging and backfilling. 	near To Kwa Wan breakwaters Construction Work	period Construction	
 transportation. The use of 300 m³ geosynthetic container, with outer woven fabric tensile strength of 200 kN/m and seam strength of 140 kN/m for effective method for contained disposal which meets ETWB TCW No. 34/2002 requirements for assuring negligible loss of contaminants to marine environment during disposal. Allocation of marine disposal sites and all necessary permits shall be applied from relevant authorities for disposal of dredged sediment. Project Proponent will obtain confirmation from CEDD/Marine Fill Committee (MFC) on the disposal options before commencement of the Project. Marine Ecology Placement of a second silt curtain between the dredger and the To Kwa Wan breakwater. The silt curtain shall be 75m long. This curtain shall be moved along with the dredger as the work progresses. The curtain shall be arranged so that at least 15m of the curtain shall ethed past the dredger in each direction. This curtain shall remain in a suitable position between the dredger and the corals until the dredger is 250m from the corals. Hazard to Life Proper general traffic management measures. Minimisation of works activity footprint – dredging and backfilling. 	near To Kwa Wan breakwaters Construction Work	period Construction	

Environmental Protection Measures	Location	Timing	Status
 The submarine gas pipeline will be covered by armour rock, damage from anchor drop could be prevented. 	Sites	period	
Landscape			
Screening of construction works by hoardings/noise barriers around Works area in visually unobtrusive colours, to screen Works.	Construction Work Sites	Construction period	N.A.
Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone).	Construction Work Sites	Construction period	N.A.
Ensure no run-off into the harbour adjacent to the site.	Construction Work Sites	Construction period	N.A.
Cultural Heritage			
A Monitoring Brief shall be conducted as set out in Appendix H2 of the EIA. This can be done in parallel with the monitoring of barge loading as set out in section 4.6.	Construction Work Sites	Construction period	\checkmark
Noise			
<u>Construction Noise Impact from Test before Backfilling and Hydrostatic/ Commissioning Test</u> The total maximum allowable SWL of the test before backfilling and hydrostatic/ commissioning test is ranged from 112-126 dB(A) at different location and period, the Contractor shall strictly follow the specification listed above to meet the noise criteria and closely liaise with the schools nearby before carrying out the activities. Noise mitigation measures including the use of movable noise barriers and/ or noise enclosure to block the direct line of sight to the receivers, installation of mufflers and/ or silencers on the machine(s) should be implemented if necessary.	Construction Work Sites (Landmain work)	Construction period	V
Using Quiet PME The use of quiet PME recognized by the Noise Control Authority for the purpose of CNP application can effectively reduce the noise generated from the construction plants. Quiet PME are construction plants and equipments that are notably quieter, more environmental friendly and efficiently. The noise level reduction ranges from 5 – 10 dB(A) depending on the type of equipment used. The Contractor should note the required procedures involved in application of the QPME. A list of QPME recommended is list in Table 10.11 of the EIA report.	Construction Work Sites (Along the alignment of dredging and landmain works)	Construction period	V
Using Movable Noise Barriers Movable noise barriers to be erected near to the construction plants would reduce the noise levels for commonly 5 – 10 dB(A) depending on the types of items of PME and materials of the barriers. It is recommended that the Contractor should screen noisy works and noise from stationary items of PME whenever practicable.	Construction Work Sites (Landmain work)	Construction period	
Good Site Practices Good Site Practices Good site practice and noise management can significantly reduce the impact of construction site activities on nearby NSRs. The following package of measures shall be followed during construction: • The Contractor shall adopt the Code of Practice on Good Management Practice to Prevent Violation of the Noise Control Ordinance (Chapter 400) (for Construction Industry) published by EPD;	Construction Work Sites (Along the alignment of dredging and landmain works)	Construction period	V
• The Contractor shall observe and comply with the statutory and non-statutory requirements and guidelines;			
 Before commencing any work, the Contractor shall submit to the Engineer Representative for approval the method of working, equipment and noise mitigation measures intended to be used at the site; 			
• The Contractor shall devise and execute working methods to minimise the noise impact on the surrounding sensitive uses, and provide experienced personnel with suitable training to ensure that those methods are implemented;			
 Unused equipment shall be turned off. Number of operating PME shall be kept to a minimum and the parallel use of noisy equipment / machinery shall be avoided; 			

vironmental Protection Measures	Location	Timing	Status
Regular maintenance of all plant and equipment; and			
Material stockpiles and other structures shall be effectively utilised as noise barriers, where practicable.			
nstruction Dust			
tigation Measures for Fugitive Dust	Construction Work	Construction	
mitigate fugitive dust impact, all dust control measures recommended in the Air Pollution Control (Construction Dust) Regulation ere applicable, shall be implemented. Relevant dust control measures include:	, Sites (General)	period	
The works area for site clearance shall be sprayed with water before, during and after the operation so as to maintain the entire surface wet;			
Restricting heights from which materials are to be dropped, as far as practicable to minimise the fugitive dust arising from unloading/ loading;			
Immediately before leaving a construction site, all vehicles shall be washed to remove any dusty materials from the bodies and wheels. However, all spraying of materials and surfaces should avoid excessive water usage;			
Where a vehicle leaving a construction site is carrying a load of dusty materials, the load shall be covered entirely by clean impervious sheeting to ensure that the dusty materials will not leak from the vehicle;			
Any stockpile of dusty materials shall be covered entirely by impervious sheeting; and/or placed in an area sheltered on the top and 4 sides; and			
All dusty materials shall be sprayed with water immediately prior to any loading, unloading or transfer operation so as to maintai the dusty materials wet.	n		

- Non-compliance of Mitigation Measures х
- Δ Deficiency of Mitigation Measures but rectified by the ContractorN.A. Not Applicable

Annex H

Waste Flow Table

The installation of submarine gas pipelines and associated facilities from To Kwa Wan to North Point for former Kai Tak Airport

Monting Summary waste Flow Table for fear 2012-2014	Monthly Summary	Waste Flow Table for Year 2012-2014
---	-----------------	-------------------------------------

	Act	Actual Quantities of Inert C&D Materials Generated Monthly (see Note 1)				Actual Quantities of C&D Wastes Generated Monthly					
Month	Total Quantity Generated	Broken Concrete (see Note 2)	Reused in the Contract	Reused in other Projects	Disposed at Public Fill	Stockpiling	General refuse	Vegetation / Rubbish	Disposal at Landfill	Chemical Waste Recycling (see Note 3)	Recycling of Rubbish
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in'000kg / '000L)	(in '000kg)
Jun 12	858.93	858.93	150	0	8.93	700	0	0	0	0	0
Jul 12	398.16	398.16	150	0	98.16	150	0	0	0	0	0
Aug 12	316.12	316.12	290	0	25.87	0	0.25	0.5	0	0	0.5
Sep 12	136.5	136.5	80.5	0	56.1	0	0.5	0.5	0	0	0.5
Oct 12	82.39	82.39	30	0	52.39	0	0.2	0.3	0	0	0.2
Nov 12	71.23	71.23	44.84	0	26.39	0	0.1	0.1	0	0	0.1
Dec 12	168.22	168.22	95.35	0	72.87	0	0.15	0.15	0	0	0.15
Jan 13	1872.19	469.54	106.92	0	1765.27	0	0.5	0.06	0.51	0	0.05
Feb 13	1838.82	477.36	238.68	0	1480.8	119.34	0.04	0	0	0.2	0
Mar 13	473.94	473.94	57.6	0	377.94	38.4	1.24	0	1.24	0	0
Apr 13	210.07	166.07	66.96	0	99.11	0	0.5	0	0	0	0
May 13	253.8	253.8	192.6	0	0	61.2	2.06	0	2.56	0	0
Jun 13	172.8	172.8	45.07	0	57.71	70.02	7.27	0	7.27	0	0
Jul 13	151.57	151.57	41.18	0	92.39	18	0.96	0	0.96	0	0
Aug 13	575.18	575.18	41.18	0	516	18	2.63	0	2.63	0	0
Sep 13	615.37	0	0	0	597.37	18	5.74	0	0	0	0
Oct 13	706.56	0	0	0	688.56	18	2.98	0	0	0	0
Nov 13	525.56	0	60.31	0	435.25	30	0	0	0	0	0
Dec 13	231.54	0	21.09	0	210.45	0	2.91	0	2.91	0	0

	Actual Quantities of Inert C&D Materials Generated Monthly (see Note 1)							Actual Quantities of C&D Wastes Generated Monthly				
Month	Total Quantity Generated	Broken Concrete (see Note 2)	Reused in the Contract	Reused in other Projects	Disposed at Public Fill	Stockpiling	General refuse	Vegetation / Rubbish	Disposal at Landfill	Chemical Waste Recycling (see Note 3)	Recycling of Rubbish	
	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in'000kg / '000L)	(in '000kg)	
Jan 14	231.54	0	126.6	0	104.94	0	3.46	0	3.46	0	0	
Feb 14	115.00	0	75.92	0	9.08	30	4.25	0	0	0	0	
Mar 14	37.80	0	30.00	0	0	7.8	4.25	0	0	0	0	
Apr 14	0	0	0	0	0	0	1.07	0	0	0	0	
Sub-total	10043.29	4771.81	1944.80	0	6775.58	1278.76	41.06	1.61	21.54	0.20	1.50	
May 14	27	0	0	0	0	0	1.12	0	0	0	0	
Total	10070.29	4771.81	1944.80	0	6775.58	1278.76	42.18	1.61	21.54	0.20	1.50	

 Notes:
 (1)
 If necessary, use the conversion factor: 1 full load of dumping truck being equivalent to 6.5 m³ by volume.

 (2)
 Broken concrete for recycling into aggregates.

 (3)
 For chemical waste, the actual quantities of empty paint cans will be in kilogram (kg) and spent lubrication oil will be in litre (L).

Annex I

Cumulative Complaint and Summons/Prosecutions Log

Reporting Month	Number of Complaints in Reporting Month	Number of Summons/Prosecutions in Reporting Month
June 2012	0	0
July 2012	0	0
August 2012	0	0
September 2012	0	0
October 2012	0	0
November 2012	0	0
December 2012	0	0
January 2013	0	0
February 2013	0	0
March 2013	0	0
April 2013	0	0
May 2013	0	0
June 2013	0	0
July 2013	0	0
August 2013	0	0
September 2013	0	0
October 2013	0	0
November 2013	0	0
December 2013	0	0
January 2014	0	0
February 2014	0	0
March 2014	0	0
April 2014	0	0
May 2014	0	0
Overall Total	0	0

Annex I Cumulative Complaint and Summons/Prosecutions Log
