# ASB Biodiesel (Hong Kong) Limited

# Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate

Monthly EM&A Report (Version 1.0)

November 2010

Certified By

(Environmental Team Leader)

## REMARKS:

The information supplied and contained within this report is, to the best of our knowledge, correct at the time of printing.

CINOTECH accepts no responsibility for changes made to this report by third parties

## CINOTECH CONSULTANTS LTD

Room 1710, Technology Park, 18 On Lai Street, Shatin, NT, Hong Kong Tel: (852) 2151 2083 Fax: (852) 3107 1388

Email: info@cinotech.com.hk

# TABLE OF CONTENTS

		Page
EXECUTIV	E SUMMARY	1
Introduction .		1
	al Monitoring and Audit Works	
	al Licenses and Permits	
Key Informat	ion in the Reporting Month	1
Future Key Is	ssues	2
1 INTRO	DUCTION	3
Background		3
Project Organ	nizations	4
Construction	Programme	4
Summary of	EM&A Requirements	4
2 ENVIR	ONMENTAL AUDIT	6
Site Audits		6
Status of Env	rironmental Licensing and Permitting	6
	ste Management	
	on Status of Environmental Mitigation Measures	
Summary of	Complaint and Prosecution	8
3 FUTUR	E KEY ISSUES	9
Kev Issues fo	or the Coming Month	9
•	Program for the Next Month	
4 CONCI	LUSIONS AND RECOMMENDATIONS	10
Conclusions .		
	ntions	
LIST OF TA	ABLES	
Table I	Summary Table for Key Information in the Reporting Month	
Table 1.1	Key Project Contacts	
Table 2.1	Summary of Environmental Licensing and Permit Status	
Table 2.2	Observations and Recommendations of Site Audit	
LIST OF FI	CURE	
DIST OF T	CORE	
Figure 1.1	Site Layout Plan	
LIST OF A	PPENDICES	
Appendix A	Site Audit Summary	
Appendix B	Updated Environmental Mitigation Implementation Schedule	
Appendix C	Waste Generation in the Reporting Month	
Appendix D	Complaint Log	
Appendix E	Construction Programme	

#### **EXECUTIVE SUMMARY**

#### Introduction

- 1. This is the 18<sup>th</sup> monthly Environmental Monitoring and Audit (EM&A) Report prepared by Cinotech Consultants Limited for Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate". This report documents the findings of EM&A Works conducted in November 2010.
- 2. The major site activities undertaken in the reporting month included:
  - Structural Steel Works, incl. material transportation, parts assembling, grating installation, painting etc;
  - General site cleaning and tidying;
  - Taking measures for preventing mosquito breeding; and
  - Site Investigation for Jetty Construction.

## **Environmental Monitoring and Audit Works**

3. Environmental monitoring and audit works for the Project were performed regularly as stipulated in the EM&A Manual and the results were checked and reviewed. The implementation of the environmental mitigation measures and environmental complaint handling procedures were also checked.

#### **Environmental Licenses and Permits**

4. Licenses/Permits granted to the Project include the Environmental Permit (EP) for the Project, An Environmental Permit No. EP-319/2009 and EP-319/2009/A was issued on 11 March 2009 and 7 April 2009 respectively. The contractor has applied for the Registration of Chemical Waste Producer (WPN-5113-839-C1186-15), Construction Noise Permit (GW-RE0561-09) and Wastewater Discharge License (WT00004508-2009).

## **Key Information in the Reporting Month**

5. Summary of key information in this reporting month is tabulated in Table I.

**Table I** Summary Table for Key Information in the Reporting Month

Event	<b>Event Details</b>		Action Taken	Status	Remark	
Event	Number	Nature	Action Taken	Status	Kemark	
Complaint received	0		N/A	N/A		
Changes to the assumptions and key construction / operation activities recorded	0		N/A	N/A		
Status of submissions under EP	1	Monthly EM&A Report for October 2010	Submitted to EPD on 24 November 2010	Verified by IEC		
Notifications of any summons & prosecutions	0		N/A	N/A		

## **Future Key Issues**

- 6. Major site activities for the coming month will include:
  - Administration Building concrete frame construction;
  - Fat Preparation Plant Room and Steam Boiler Room concrete frame construction;
  - GTW Separation Room ELS & Pump Test & Foundation Inspection;
  - Jetty Pre-drilling; and
  - Jetty Bored Piling.
- 7. The future environmental concerns are air quality, waste management and surface runoff from construction works.

#### 1 INTRODUCTION

## **Background**

- 1.1 Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate is a Designated Project (hereafter referred to as "the Project") under the Environmental Impact Assessment Ordinance (Cap. 449). A study of environmental impact assessment (EIA) was undertaken to consider the key issues of air quality, noise, water quality, ecological and identify possible mitigation measures associated with the works. An EIA Report was approved by the Environmental Protection Department (EPD) on 26 February 2009.
- 1.2 The project is to construct and operate a 100,000 tonnes per annum biodiesel plant at Tseung Kwan O Industrial Estate. The plant will use a multi-feedstock which consists of waste cooking oil (WCO), oil and grease recovered from grease trap waste (GTW), Palm Fatty Acid Distillate (PFAD) and animal fats. The proposed biodiesel plant not only offers a convenient recycling outlet for GTW and WCO but also converts the oil and grease recovered from these wastes into useful products. The Project also offers a cleaner alternative to diesel fuel to the Hong Kong market. The main processes include the followings:-
  - Construction of feedstock reception and storage facilities, and offices;
  - Construction of a grease trap waste pre-treatment facility (with a designated treatment capacity of about 200,000 tonnes per annum);
  - Construction of a wastewater treatment plant (with a designed treatment capacity of about 170,000 m3 per annum);
  - Installation of biodiesel production and glycerine purification system;
  - Construction of product storage and ancillary facilities;
  - Pretreatment of grease trap waste;
  - Treatment of wastewater generated from feedstock pre-treatment and glycerine dewatering process, and filtrates from dewatering process of sludge treatment;
  - Transesterification of feedstock with alcohol-catalyst; and
  - Purification of biodiesel.
  - 1.3 The general layout of the Project is shown in **Figure 1.1.**
  - 1.4 Layout plan of tank farm **2A**, **2B** to **2E** is revised and a report is made by Environmental Resources Management (ERM) regarding such change. The report concluded that no deviation is found from the approved EIA report.
  - 1.5 An Environmental Permit (EP) No. EP-319/2009 and EP-319/2009/A was issued on 11 March 2009 and 7 April 2009 respectively for Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate to ASB Biodiesel (Hong Kong) Limited as the Permit Holder.
  - 1.6 Cinotech Consultants Limited was commissioned by ASB Biodiesel (Hong Kong) Limited to undertake the Environmental Monitoring and Audit (EM&A) works for the Project. China Harbour Engineering Company Limited is the Managing Contractor of

the Project. This is the 18<sup>th</sup> Monthly EM&A report summarizing the EM&A works for the Project in November 2010.

## **Project Organizations**

- 1.7 Different parties with different levels of involvement in the project organization include:
  - Project Proponent ASB Biodiesel (Hong Kong) Limited
  - Contractor China Harbour Engineering Company Limited (CHEC)
  - Environmental Team (ET) Cinotech Consultants Limited
  - Independent Environmental Checker (IEC) Mannings (Asia) Consultants Ltd.
- 1.8 The responsibilities of respective parties are detailed in Section 1.10 of the Final EM&A Manual of the Project.
- 1.9 The key contacts of the Project are shown in Table 1.1.

Table 1.1 Key Project Contacts

Party	Role	Name	Position	Phone No.	Fax No.	
ASB	Permit Holder	Mr. Eddie Chung	Project Manager	9189 8118	37411661	
		Dr. HF Chan	ET Leader	2151 2088		
Cinotech	Environmental Team	Ms. Ivy Tam	Project Coordinator	2151 2090	3107 1388	
		Mr. Gary Lau	Audit Team Leader	2151 2098		
Mannings	Independent Environmental	Mr. Mark Cheung	Independent Environmental Checker	3168 2028	3168 2022	
Mannings	Checker	Mr. Gavin Kwok	Assistant to Independent Environmental Checker	3168 2028	3108 2022	
CHEC	Contractor	Mr. Peter Chung	Project Manager	9471 2438	2623 9226	
CHEC	Contractor	Mr. Daniel Leung	Environmental Supervisor	9877 4288	2023 9220	

#### **Construction Programme**

- 1.10 The site activities undertaken in the reporting month were:
  - Structural Steel Works, incl. material transportation, parts assembling, grating installation, painting etc;
  - General site cleaning and tidying;
  - Taking measures for preventing mosquito breeding; and
  - Site Investigation for Jetty Construction.

## **Summary of EM&A Requirements**

- 1.11 The EM&A requirements are described in the following sections, including:
  - Environmental mitigation measures, as recommended in the project EIA study final report; and
  - Environmental requirements in contract documents.

1.12 The advice on the implementation status of environmental protection and pollution control/mitigation measures is summarized in Section 3 of this report.

#### 2 ENVIRONMENTAL AUDIT

#### **Site Audits**

- 2.1 Site audit was carried out by ET on monthly basis to monitor the timely implementation of proper environmental management practices and mitigation measures in the Project site. The summaries of site audits are attached in **Appendix A**.
- 2.2 Site audit was conducted on 24<sup>th</sup> November 2010 by ET in the reporting month. No non-compliance was observed during the site audits.

## **Status of Environmental Licensing and Permitting**

2.3 All permits/licenses obtained for the Project are summarized in **Table 2.1**.

## **Status of Waste Management**

2.4 10m³ of general refuse, no Inert Construction and Demolition (C&D) Waste and no Chemical Waste are generated in the reporting month. The quantities of waste generated in this reporting month are summarized in **Appendix C**.

## **Implementation Status of Environmental Mitigation Measures**

2.5 According to the EIA Study Report, Environmental Permit and the EM&A Manual of the Project, the mitigation measures detailed in the documents are recommended to be implemented during the construction phase. An updated summary of the EMIS is provided in **Appendix B**.

 Table 2.1
 Summary of Environmental Licensing and Permit Status

Permit / License No.	Valid Period		- Details	Status	
Permit / License No.	From	To	Details	Status	
<b>Environmental Permit (EP)</b>	)				
EP-319/2009/A	07/04/2009	N/A	Construction and operation of	Valid	
			(i) a biochemical plant with a storage capacity of more than 500 tonnes and in which substances are processed and produced;		
			(ii) a storage, transfer and transhipment of oil facility with a storage capacity of not less than 1,000 tonnes; and		
			(iii) a dangerous goods godown with a storage capacity exceeding 500 tonnes		
Registration of Chemical Was	L te Producer				
WPN-5113-839-C1186-15	12/06/2009	-	Spent Lubrication oil.	Valid	
<b>Construction Noise Permit (C</b>	NP)				
GW-RE0561-09	10/12/2009	26/05/2011	Use of Powered Mechanical Equipment during 0000-2400 hours on general holidays (including Sundays), 0000-0700 hours on any day not being a general holiday.	Valid	
Wastewater Discharge License	e				
WT00004508-2009	07/09/2009	-	-	Valid	

2.6 During site inspections in the reporting month, no non-conformance was identified. The observations and recommendations made during the audit sessions are summarized in Table 2.2.

Table 2.2 Observations and Recommendations of Site Audit

Parameters	Date	<b>Observations and Recommendations</b>	Follow-up
	24/11/2010	No Major Environmental Deficiency was	
	_ ,, _ ,, _ ,	Observed During Site Inspection.	

## **Summary of Complaint and Prosecution**

- 2.7 No environmental related complaint, prosecution or notification of summons was received in the reporting month.
- 2.8 There was no environmental complaint, prosecution or notification of summons received since the Project commencement. The Complaint Log is attached in **Appendix D**.

#### **3 FUTURE KEY ISSUES**

## **Key Issues for the Coming Month**

- 3.1 Key issues to be considered in the coming month include:
  - Noise from operation of the equipment and machinery on-site;
  - Effluent discharge generated from surface runoff;
  - Dust generated from excavation works and stockpile of dusty materials;
  - Maintenance of de-silting facilities and drainage system, such as U-channels;
  - Storage of chemicals/fuel and chemical waste/waste oil on site;
  - · Accumulation of stagnant water in the site areas; and
  - Accumulation of C&D waste and general waste on site.

## **Construction Program for the Next Month**

- 3.2 A tentative construction programme is provided in **Appendix E**. The major construction activities in the coming month will include:
  - Administration Building concrete frame construction
  - Fat Preparation Plant Room and Steam Boiler Room concrete frame construction
  - GTW Separation Room ELS & Pump Test & Foundation Inspection
  - Jetty Pre-drilling
  - Jetty Bored Piling

#### 4 CONCLUSIONS AND RECOMMENDATIONS

#### **Conclusions**

- 4.1 Environmental audit works were conducted in the reporting month. Site inspections were conducted on a monthly basis. The results of were reviewed and checked.
- 4.2 There was no environmental complaint, prosecution or notification of summons received.

#### Recommendations

4.3 According to the environmental audit performed in the reporting month, the following recommendations were made:

## Water Impact

- To identify any wastewater discharges from site.
- To ensure properly maintenance for de-silting facilities.
- To clear the silt and sediment in the sedimentation tanks.
- To review the capacity of de-silting facilities for discharge.
- To divert all the water generated from construction site to de-silting facilities with enough handling capacity before discharge.
- To avoid accumulation of stagnant and ponding water on site.
- To clear the drainage channel regularly to prevent blockage.

## **Dust Impact**

- To remove fugitive dusty material on the haul road periodically.
- Excavated dusty materials or stockpile of dusty materials should be covered by impervious sheeting, or sprayed with water so as to maintain entire surface wet.


## Noise Impact

- To space out noisy equipment and position as far away as possible from sensitive receivers.
- To inspect the noise sources inside the site.

#### Waste / Chemical Management

- To provide proper rubbish bins / skips for waste collection.
- To provide proper storage area for oil container on site.
- To avoid and check for any accumulation of waste materials or rubbish on site.
- To avoid any discharge or accidental spillage of chemical waste or oil directly from the equipment.

# **FIGURES**

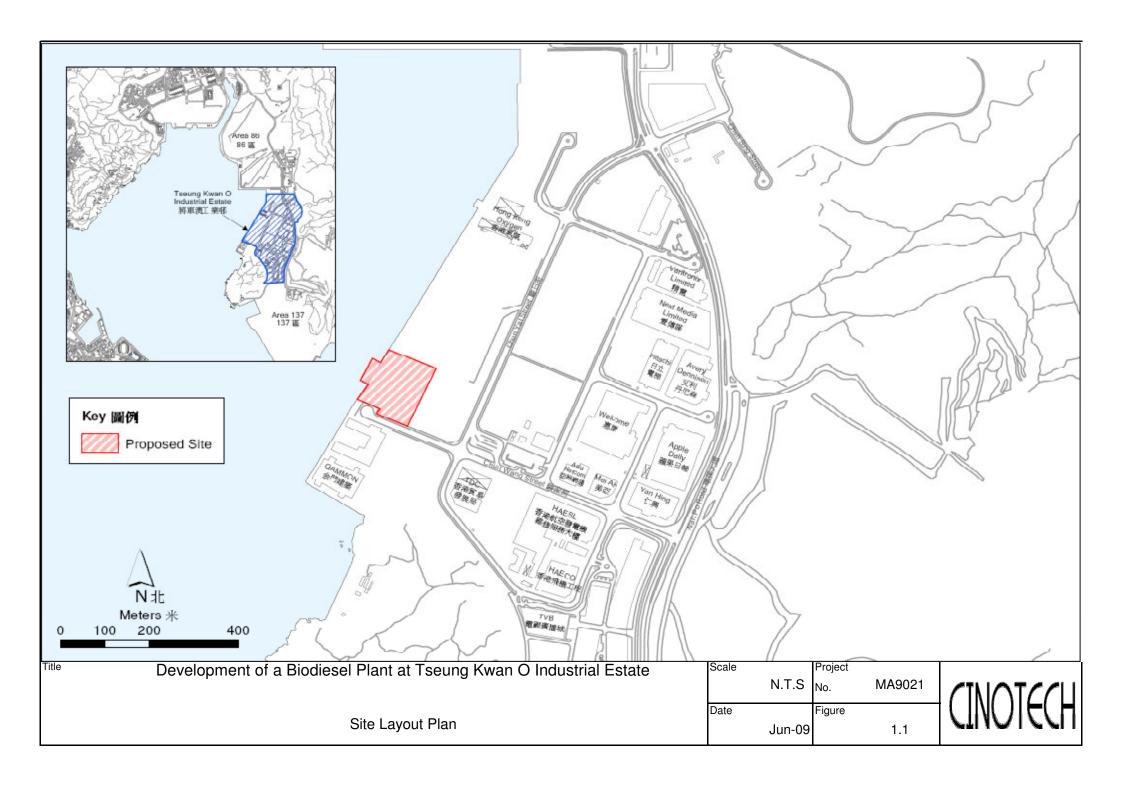

## APPENDIX A SITE AUDIT SUMMARY

# Development of a Biodiesel Plant at Tseung Kwan O Industrial Estate

## Monthly Site Inspection Record Summary

Inspection Information

Checklist Reference Number	001124
Date	24 October 2010 (Wednesday)
Time	14:30 – 15:30

Ref. No.	Non-Compliance	Related Item No.
-	None	

Ref. No.	Remarks/Observations	Related Item No.
	A. Water Quality	
	No environmental deficiency was identified during site inspection.	
	B. Air Quality	
	No environmental deficiency was identified during site inspection.	
	C. Noise	
	No environmental deficiency was identified during site inspection.	
	D. Waste / Chemical Management	
	No environmental deficiency was identified during site inspection.	
	E. Permit / Licenses	
	No environmental deficiency was identified during site inspection.	
	F. Reminders	
	No environmental deficiency was identified during site inspection.	
	G. Others	
	• Follow-up on previous audit section (Ref. No.:001022), all environmenta	1
	deficiencies were improved/rectified by contractor.	

	Name	Signature	Date
Recorded by	Gary Lau	Ban L.	30 November 2010
Checked by	Dr. HF Chan	M	30 November 2010

CINOTECH MA9021 001124

APPENDIX B UPDATED ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE

Appendix B - Summary of Environmental Mitigation Implementation Schedule (Construction Phase)

Types of Impacts	Mitigation Measures	Status
	• Dust control measures such as water spaying on roads and dusty areas, covering of lorries by impervious sheets and controlling of the falling height of fill materials will be implemented;	٨
	• Effective dust screens, sheeting or netting will be provided to enclose the scaffolding from the ground level of the facility during the building construction;	N/A
	<ul> <li>All debris and materials will be covered or stored in a sheltered debris collection area;</li> </ul>	^
Construction Dust	<ul> <li>Hoarding from ground level will be provided along the entire length of the site boundary except for a site entrance or exit;</li> <li>Every stockpile of dusty materials will be covered entirely by impermeable sheeting or placed in an area sheltered on the top</li> </ul>	^
	<ul> <li>and the 3 sides;</li> <li>Regular maintenance and checking of the diesel powered mechanical equipment will be adopted to avoid any black smoke</li> </ul>	^
	emissions and to minimize gaseous emissions.	^
	• Monthly site audits will be conducted to ensure the implementation of suitable dust control measures and good site practices.	^
	Only well-maintained plant will be operated on-site and plant will be serviced regularly during the construction program;	^
	<ul> <li>Silencers or mufflers on construction equipment will be utilized and will be properly maintained during the construction program;</li> </ul>	^
	<ul> <li>Mobile plant, if any, will be sited as far from NSRs as possible;</li> </ul>	^
Construction	<ul> <li>Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or will be throttled down to a minimum;</li> </ul>	^
Noise	• Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and	^
	<ul> <li>Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from onsite construction activities.</li> </ul>	^

Types of Impacts	Mitigation Measures	Status
	<ul> <li>Silt curtain will be installed around the marine piling area to contain any suspended mud and sediments generated during the piling works. Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from groundwater (if pumping is required) to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.</li> <li>Construction Site Run-off and Drainage</li> </ul>	N/A
Water Quality	• Silt removal facilities such as silt traps or sedimentation facilities will be provided to remove silt particles from runoff to meet the requirements of the TM standard under the WPCO. The design of silt removal facilities will be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures will be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.	٨
water Quanty	<ul> <li>Careful programming of the works to minimise surface excavations for the construction works during the wet season. If excavation of soil cannot be avoided during the wet season, exposed slope surfaces will be covered by a tarpaulin or other means. Other measures that need to be implemented before, during, and after rainstorms are summarised in ProPECC PN 1/94.</li> <li>Exposed soil surfaces will be protected by paving or fill material as soon as possible to reduce the potential of soil erosion.</li> <li>Open stockpiles of construction materials or construction wastes on site of more than 50m3 will be covered with tarpaulin or</li> </ul>	^
	<ul> <li>Open stockpiles of construction materials or construction wastes on-site of more than 50m3 will be covered with tarpaulin or similar fabric during rainstorms. These materials will not be placed near the seawall area.</li> <li>General Construction Activities</li> <li>Debris and refuse generated on-site will be collected, handled and disposed of properly to avoid entering the nearby water sensitive receivers (WSRs). Stockpiles of cement and other construction materials will be kept covered when not being used.</li> <li>Oils and fuels will only be used and stored in designated areas which have pollution prevention facilities. All fuel tanks and storage areas will be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund will be drained of rainwater after a rain event.</li> </ul>	^

Types of Impacts	Mitigation Measures	Status
Sewage generated from On-site Workforce		
	<ul> <li>Temporary sanitary facilities, such as portable chemical toilets, will be provided on-site. A specialised contractor will be responsible for regular collection and appropriate disposal of the sewage and maintenance of these facilities.</li> <li>Monthly site inspections will be carried out during construction to ensure that the mitigation measures listed above are properly implemented. The site audit frequency will be increased to weekly intervals during the piling works.</li> </ul>	N/A
Ecology	Mitigation measures for minimising water quality impacts are presented in detail above. These measures will be properly implemented and good construction practices will be adopted to minimise potential adverse impacts to marine ecological resources.	^

Remarks: ^

- ^ Compliance of mitigation measure; X Non-compliance of mitigation measure;
  N/A Not Applicable at this stage; Non-compliance but rectified by the contractor;
  Recommendation was made during site audit but improved/rectified by the contractor;
  Non-compliance but rectified/improved by the contractor and awaiting IEC's further comment.

APPENDIX C WASTE GENERATION IN THE REPORTING MONTH Monthly Summary Waste Flow Table For Contract 250 Biodiesel Plant Tseung Kwan O Project Reporting Year: <u>2010</u>

	Actual Quantities of Inert C&D Materials Generated / Imported (in '000 m³)						Actual Quantities of Other C&D Materials / Wastes Generated				
Month	Total Quantities Generated [a+b+c+d]	Broken Concrete (including rock for recycling into aggregates) (a)	Reused in the Contract	Reused in Other Projects ( c )	Disposed as Public Fill (d)	Imported C&D Material	Metal (in '000 kg)	Paper/ cardboard packaging (in '000kg)	Plastics (bottles/containers, plastic sheets/ foams from package material) (in '000kg)	Chemical Waste (in '000kg)	Others (e.g. General Refuse etc.) (in '000m3)
January	0.001	0	0	0	0.001	0	0	0.05	0.01	0	0.02
February	0	0	0	0	0	0	0	0.05	0.01	0	0.02
March	0.01	0	0	0	0.01	0	0	0.05	0.01	0	0.02
April	0	0	0	0	0	0	0	0.01	0.01	0	0.02
May	0	0	0	0	0	0	0	0.01	0.01	0	0.02
June	0	0	0	0	0	0	0	0.02	0.01	0	0.02
Half-year Total	0.01	0	0	0	0.01	0	0	0.19	0.06	0	0.12
July	0	0	0	0	0	0	0	0.01	0.01	0	0.02
August	0	0	0	0	0	0	0	0.01	0.01	0	0.01
September	0	0	0	0	0	0	0	0	0.	0	0.002
October	0.02	0.02	0	0	0	0	0	0	0	0	0.01
November	0	0	0	0	0	0	0	0	0	0	0.01
December											
Yearly Total											

## APPENDIX D COMPLAINT LOG

## APPENDIX D - COMPLAINT LOG

**Reporting Month**: November 2010

Log Ref.	Log Ref. Location		Details of Complaint	Investigation/Mitigation Action	Status	
N/A	N/A	N/A	N/A	N/A	N/A	

Remarks: No environmental complaint was received in the reporting month.

# APPENDIX E CONSTRUCTION PROGRAMME

File Name: C250-EP-R02\_(Dec 10)\_Partial Commencement.mpp Baseline: C-250-EP-R01\_(June 2010)\_BC (Date:14 June 2010)

# Proposed Bio-Diesel Plant at T.K.O.T. Lot No. 39 S.Q. ss.1, ss.2 and Ext. thereto Chun Wang Street, TKO Ind. Estate, Kln Master Programme Dec 10 Update (With Partial Recommencement by Jan 11 and Full Remommencement by Apr 11)

Section	Task Name	Duration	Current Start	Current	2010	2011 2012
5 (	Construction Works	643 days	3/4/10			2 1 2 3 4 5 6 7 8 9 10 11 2 1 2 3 4 5 6 7 8 9 5/1
5.1	1A - Administration Building	324 days	2/1/11	21/11/11	2/1	21/11
5.1.1	Superstructure Construction Works	114 days	2/1/11	25/4/11		0%
5.2	1B - Process Building	598 days	3/4/10	21/11/11	3/4	21/11
5.6	2A - GTW Separation Room	324 days	2/1/11	21/11/11	2/1	21/11
5.6.1	ELS & Pump Test & Formation Inspection	84 days	2/1/11	26/3/11		0%
5.9	4A - Jetty	462 days	1/10/10	5/1/12	1/10	<b>□</b> 5/1
5.9.1	SI and Founding Level determination (Includind BD Submission)	97 days	1/10/10	5/1/11		70%
5.9.2	Piling Stage 1 (SW Pump House Side)	152 days	24/1/11	24/6/11		0%
	5.1 5.1.1 5.2 5.6 5.6.1 5.9	5.1.1 Superstructure Construction Works  5.2 1B - Process Building  5.6 2A - GTW Separation Room  5.6.1 ELS & Pump Test & Formation Inspection  5.9 4A - Jetty  5.9.1 SI and Founding Level determination (Includind BD Submission)	5 Construction Works 643 days  5.1 1A - Administration Building 324 days  5.1.1 Superstructure Construction Works 114 days  5.2 1B - Process Building 598 days  5.6 2A - GTW Separation Room 324 days  5.6.1 ELS & Pump Test & Formation Inspection 84 days  5.9 4A - Jetty 462 days  5.9.1 SI and Founding Level determination (Includind BD Submission) 97 days	5 Construction Works       643 days       3/4/10         5.1 1A - Administration Building       324 days       2/1/11         5.1.1 Superstructure Construction Works       114 days       2/1/11         5.2 1B - Process Building       598 days       3/4/10         5.6 2A - GTW Separation Room       324 days       2/1/11         5.6.1 ELS & Pump Test & Formation Inspection       84 days       2/1/11         5.9 4A - Jetty       462 days       1/10/10         5.9.1 SI and Founding Level determination (Includind BD Submission)       97 days       1/10/10	5 Construction Works       643 days       3/4/10       Finish         5.1       1A - Administration Building       324 days       2/1/11       21/11/11         5.1.1       Superstructure Construction Works       114 days       2/1/11       25/4/11         5.2       1B - Process Building       598 days       3/4/10       21/11/11         5.6       2A - GTW Separation Room       324 days       2/1/11       21/11/11         5.6.1       ELS & Pump Test & Formation Inspection       84 days       2/1/11       26/3/11         5.9       4A - Jetty       462 days       1/10/10       5/1/12         5.9.1       SI and Founding Level determination (Includind BD Submission)       97 days       1/10/10       5/1/11	5 Construction Works 643 days 5/1/12 5.1 1A - Administration Building 5.1 1A - Administration Building 5.1 1Superstructure Construction Works 114 days 114 days 115 days 116 7 8 9 10111 21/11/1
