
Report



Contract No. HY/2012/08
Tuen Mun – Chek Lap Kok Link –
Northern Connection Sub-sea Tunnel
Section

Seventh Quarterly Environmental Monitoring & Audit (EM&A) Report

06 January 2016

Environmental Resources Management

16/F, Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone 2271 3000 Facsimile 2723 5660

www.erm.com





Ref.: HYDHZMBEEM00_0_3741L.16

11 January 2016

AECOM
Supervising Officer Representative's Office
No.8 Mong Fat Street, Tuen Mun,
New Territories, Hong Kong

By Fax (2293 6300) and By Post

Attention: Messrs. Edwin Ching / Andy Westmoreland

Dear Sirs,

Re: Agreement No. CE 48/2011 (EP)
Environmental Project Office for the
HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing
Facilities, and Tuen Mun-Chek Lap Kok Link – Investigation

Contract No. HY/2012/08 TM-CLKL Northern Connection Sub-sea Tunnel Section
Seventh Quarterly EM&A Report

Reference is made to the Quarterly Environmental Monitoring and Audit (EM&A) Report (June to Aug. 2015) (ET's ref.: "0212330_7th Quarterly EM&A_20151221.doc" dated 6 Jan. 2016) certified by the ET Leader and provided to the IEC via e-mail on 6 Jan. 2016.

We are pleased to inform you that we have no adverse comments on the captioned quarterly EM&A report.

Thank you for your kind attention. Please do not hesitate to contact the undersigned or the ENPO Leader Mr. Y. H. Hui should you have any queries.

Yours sincerely,

F. C. Tsang

Independent Environmental Checker

Tuen Mun – Chek Lap Kok Link

c.c.

HyD - Mr. Stephen Chan (By Fax: 3188 6614) HyD - Mr. Matthew Fung (By Fax: 3188 6614) AECOM - Mr. Conrad Ng (By Fax: 3922 9797) ERM - Mr. Jovy Tam (By Fax: 2723 5660)

Dragages - Bouygues JV - Mr. C. F. Kwong (By Fax: 2293 7499)

Internal: DY, YH, LP, CL, ENPO Site

Q:\Projects\HYDHZMBEEM00\02_Proj_Mgt\02_Corr\HYDHZMBEEM00_0_3741L.16.docx



Contract No. HY/2012/08 Tuen Mun – Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section

Seventh Quarterly Environmental Monitoring & Audit (EM&A) Report

Document Code: 0212330_7th Quarterly EM&A_20151221.doc

Environmental Resources Management

16/F, Berkshire House 25 Westlands Road Quarry Bay, Hong Kong Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

Summary: Date: 06 January 2016 Approved by: This document presents the Seventh Quarterly EM&A Report for Tuen Mun – Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section. Mr Craig Reid Partner Certified by: Mr Jovy Tam ET Leader 7th Quarterly EM&A Report Revision Description This report has been prepared by Environmental Resources Management the trading name of IERM Hong-Kong, Limited", with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.	Client:		Project N	0:				
This document presents the Seventh Quarterly EM&A Report for Tuen Mun – Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section. Mr Craig Reid Partner Certified by: Mr Jovy Tam ET Leader This quarterly EM&A Report VAR JT CAR 06/01/16 Revision Description This report has been prepared by Environmental Resources Management the trading name of ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.	DBJV		0212330					
Mr Craig Reid Partner Certified by: Mr Jovy Tam ET Leader 7th Quarterly EM&A Report VAR JT CAR 06/01/16 Revision Description By Checked Approved Date This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.	This document presents the Seventh Quarterly EM&A Report for Tuen Mun – Chek Lap Kok Link Northern Connection Sub-sea			06 January 2016				
Revision Description By Checked Approved Date This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. Distribution Internal Public Confidential				Partner Certified by: Mr Jovy Tam				
Revision Description By Checked Approved Date This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. Distribution Internal Public Confidential								
This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. Distribution Internal Public Confidential		7 th Quarterly EM&A Report	VAR	JT	CAR	06/01/16		
This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. Public Confidential	Revision	Description	Ву	Checked	Approved	Date		
	'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the			Distribution Internal OHSAS 18001:2007 Certificate No. OHS 515 Public Confidential JSO 9001: 2008				



TABLE OF CONTENTS

	EXECUTIVE SUMMARY	Ι
1	INTRODUCTION	1
1.1	BACKGROUND	1
1.2	SCOPE OF REPORT	2
1.3	ORGANIZATION STRUCTURE	2 2
1.4	SUMMARY OF CONSTRUCTION WORKS	3
2	EM&A RESULTS	5
2.1	AIR QUALITY	5
2.2	WATER QUALITY MONITORING	8
2.3	DOLPHIN MONITORING	9
2.4	EM&A SITE INSPECTION	15
2.5	Waste Management Status	18
2.6	ENVIRONMENTAL LICENSES AND PERMITS	19
2.7	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	21
2.8	SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMA	NCE
	LIMIT	21
2.9	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL	
	PROSECUTIONS	23
3	FUTURE KEY ISSUES	24
3.1	CONSTRUCTION ACTIVITIES FOR THE COMING QUARTER	24
3.2	KEY ISSUES FOR THE COMING QUARTER	24
3.3	MONITORING SCHEDULE FOR THE COMING QUARTER	24
4	CONCLUSIONS	25

APPENDIX A PROJECT ORGANIZATION

APPENDIX B CONSTRUCTION PROGRAMME

APPENDIX C ENVIRONMENTAL MITIGATION AND

ENHANCEMENT MEASURE IMPLEMENTATION

SCHEDULES (EMIS)

APPENDIX D ACTION AND LIMIT LEVELS

APPENDIX E MONITORING SCHEDULE

APPENDIX F AIR QUALITY MONITORING RESULTS

APPENDIX G WATER QUALITY MONITORING RESULTS

APPENDIX H IMPACT DOLPHIN MONITORING

APPENDIX I EVENT AND ACTION PLAN

APPENDIX J CUMULATIVE STATISTICS ON EXCEEDANCE AND

COMPLAINT

APPENDIX K WASTE FLOW TABLE

EXECUTIVE SUMMARY

Under *Contract No. HY/2012/08*, Dragages – Bouygues Joint Venture (DBJV) is commissioned by the Highways Department (HyD) to undertake the design and construction of the Northern Connection Sub-sea Tunnel Section of the Tuen Mun – Chek Lap Kok Link Project (TM-CLK Link Project) while AECOM Asia Company Limited was appointed by HyD as the Supervising Officer. For implementation of the environmental monitoring and audit (EM&A) programme under the Contract, ERM-Hong Kong, Limited (ERM) has been appointed as the Environmental Team (ET) in accordance with *Environmental Permit No. EP-354/2009/A*. Ramboll Environ Hong Kong Ltd. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO). Subsequent applications for variation of environmental permits (VEP), *EP-354/2009/B*, *EP-354/2009/C and EP-354/2009/D*, were granted on 28 January 2014, 10 December 2014 and 13 March 2015, respectively.

The construction phase of the Project commenced on 1 November 2013 and will tentatively be completed by the end of 2018. The impact monitoring of the EM&A programme, including air quality, water quality, marine ecological monitoring and environmental site inspections, were commenced on 1 November 2013.

This is the Seventh Quarterly EM&A report presenting the EM&A works carried out during the period from 1 June 2015 to 31 August 2015 for the *Contract No. HY/2012/08 Northern Connection Sub-sea Tunnel Section* (the "Project") in accordance with the Updated EM&A Manual of the TM-CLK Link Project. As informed by the Contractor, the major activities in the reporting quarter included:

Land-based Works

- Surcharge Removal at Works Area Portion N-C;
- Box Culvert Extension at Works Area Portion N-A;
- Excavation for Ventilation Shaft at Works Area Portion N-C;
- Startup of TBM at Works Area Portion N-A;
- Delivery & Assembly of TBM at Works Area Portion N-A;
- Set up of Slurry Treatment Plant at Works Area Portion N-C;
- Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C;
- Installation of Tower Crane at Works Area Portion N-C;
- TBM Tunnel Works at Works Area Portion N-B; and
- Modification and Maintenance Works for Slurry Treatment Plant at Works Area Portion N-C.

A summary of monitoring and audit activities conducted in the reporting period is listed below:

24-hour TSP Monitoring 31 sessions

1-hour TSP Monitoring 31 sessions

Impact Water Quality Monitoring 3 sessions

Impact Dolphin Monitoring 6 sessions

Joint Environmental Site Inspection 13 sessions

Implementation of Marine Mammal Exclusion Zone

There was no dredging, reclamation or marine sheet piling works in open waters during this reporting period. Thus, Passive Acoustic Monitoring (PAM) and the day-time monitoring of Dolphin Exclusion Zone (DEZ) by dolphin observers were not in effect during the reporting period.

Summary of Breaches of Action/Limit Levels

Breaches of Action and Limit Levels for Air Quality

No exceedances were recorded from the air quality monitoring in this reporting period.

Breaches of Action and Limit Levels for Water Quality

No exceedances were recorded from the water quality monitoring in this reporting period.

Dolphin Monitoring

Whilst one Limit Level exceedance was observed for the quarterly dolphin monitoring data between June 2015 and August 2015, no unacceptable impact from the construction activities of the TM-CLKL Northern Connection Sub-sea Tunnel Section on Chinese White Dolphins was noticeable from general observations during the dolphin monitoring in this reporting quarter.

Environmental Complaints, Non-compliance & Summons

No non-compliance with EIA recommendations, EP conditions and other requirements associated with the construction of this Contract was recorded in this reporting period.

No environmental complaint was received in this reporting period.

No environmental summons was received in this reporting period.

Reporting Change

There was no reporting change required in the reporting period.

Upcoming Works for the Next Reporting Period

Works to be undertaken in the coming quarterly period include the following:

Land-based works

- Box Culvert Extension at Works Area Portion N-A;
- Installation of Tower Crane at Works Area Portion N-C;
- Base Slab Construction for Ventilation Shaft at Works Area Portion N-C;
- TBM Tunnel Works at Works Area Portion N-B; and
- Modification and Maintenance Works for Slurry Treatment Plant at Works Area – Portion N-C.

Future Key Issues

Potential environmental impacts arising from the above upcoming construction activities in the coming quarterly period are expected to be mainly associated with dust, marine water quality, marine ecology and waste management.

As informed by the Contractor, Phase I Reclamation works for the Northern Landfall was substantially completed in December 2014, a proposal letter was sent to EPD on 21 May 2015 to seek approval for the temporary suspension of Water Quality Monitoring. Subsequently, a letter from EPD on 5 June 2015 stated that they have no strong objection to the temporary suspension of the water quality monitoring. Water Quality Monitoring was suspended from 6 June 2015 effectively and will resume when Phase II Reclamation commences in the fourth quarter of 2016 tentatively.

INTRODUCTION

1.1 BACKGROUND


1

According to the findings of the Northwest New Territories (NWNT) Traffic and Infrastructure Review conducted by the Transport Department, Tuen Mun Road, Ting Kau Bridge, Lantau Link and North Lantau Highway would be operating beyond capacity after 2016. This forecast has been based on the estimated increase in cross boundary traffic, developments in the Northwest New Territories (NWNT), and possible developments in North Lantau, including the Airport developments, the Lantau Logistics Park (LLP) and the Hong Kong – Zhuhai – Macao Bridge (HZMB). In order to cope with the anticipated traffic demand, two new road sections between NWNT and North Lantau – Tuen Mun – Chek Lap Kok Link (TM-CLKL) and Tuen Mun Western Bypass (TMWB) are proposed.

An Environmental Impact Assessment (EIA) of TM-CLKL (the Project) was prepared in accordance with the EIA Study Brief (No. ESB-175/2007) and the *Technical Memorandum of the Environmental Impact Assessment Process (EIAO-TM*). The EIA Report was submitted under the Environmental Impact Assessment Ordinance (EIAO) in August 2009. Subsequent to the approval of the EIA Report (EIAO Register Number AEIAR-146/2009), an Environmental Permit (EP-354/2009) for TM-CLKL was granted by the Director of Environmental Protection (DEP) on 4 November 2009, and EP variation (VEP) (EP-354/2009A) was issued on 8 December 2010. Subsequent applications for variation of environmental permits (VEP), *EP-354/2009/B*, *EP-354/2009/C* and *EP-354/2009/D*, were granted on 28 January 2014, 10 December 2014 and 13 March 2015, respectively.

Under *Contract No. HY/2012/08*, Dragages – Bouygues Joint Venture (DBJV) is commissioned by the Highways Department (HyD) to undertake the design and construction of the Northern Connection Sub-sea Tunnel Section of TM-CLKL while AECOM Asia Company Limited was appointed by HyD as the Supervising Officer. For implementation of the environmental monitoring and audit (EM&A) programme under the Contract, ERM-Hong Kong, Limited (ERM) has been appointed as the Environmental Team (ET) in accordance with Environmental Permit No. EP-354/2009/A. Ramboll Environ Hong Kong Ltd. was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO).

Layout of the Contract components is presented in *Figure 1.1*.

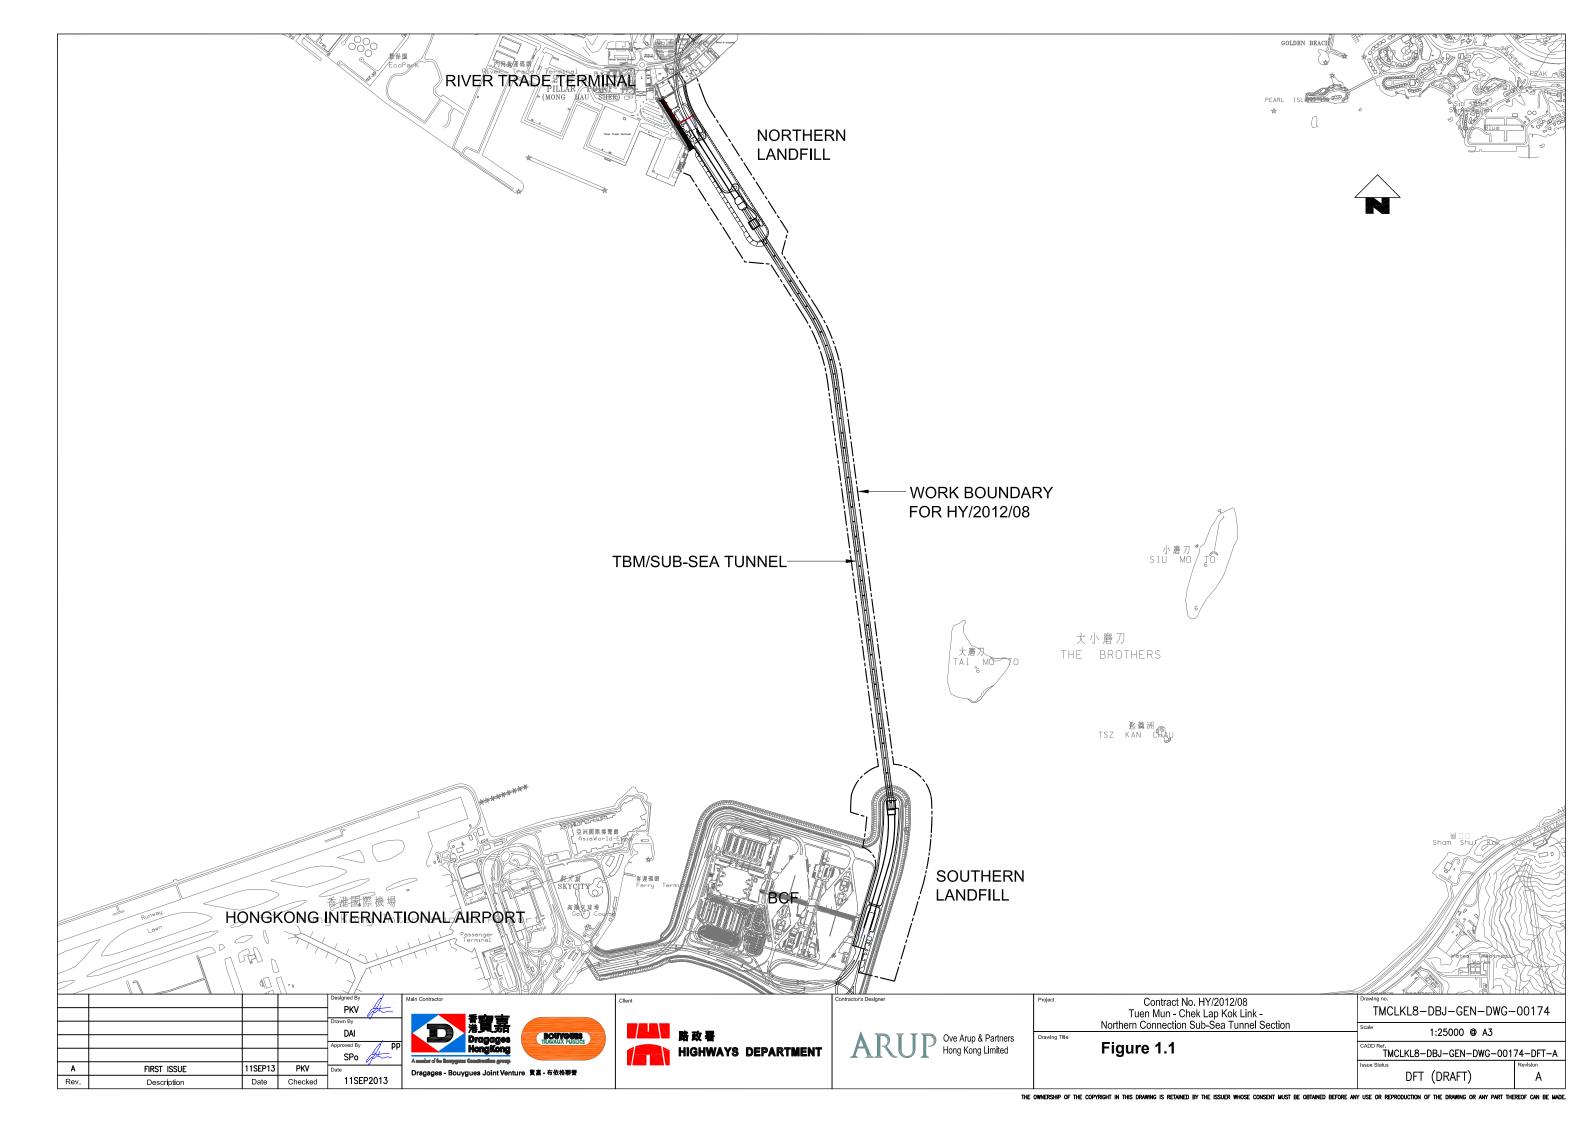

The construction phase of the Contract commenced on 1 November 2013 and will tentatively be completed by 2018. The impact monitoring phase of the EM&A programme, including air quality, water quality, marine ecological monitoring and environmental site inspections, were commenced on 1 November 2013.

1.2 Scope of Report

This is the Seventh Quarterly EM&A Report under the *Contract No. HY/2012/08 Tuen Mun – Chek Lap Kok Link – Northern Connection Sub-sea Tunnel Section.* This report presents a summary of the environmental monitoring and audit works from 1 June 2015 to 31 August 2015.

1.3 ORGANIZATION STRUCTURE

The organization structure of the Contract is shown in *Appendix A*. The key personnel contact names and contact details are summarized in *Table 1.1* below.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name	Telephone	Fax
Highways Department	Engr 16/HZMB	Kenneth Lee	2762 4996	3188 6614
SOR (AECOM Asia Company	Chief Resident Engineer	Edwin Ching	2450 3111	2450 3099
Limited)	0	Andrew Westmoreland	2450 3511	2450 3099
ENPO / IEC (Ramboll Environ Hong	ENPO Leader	Y.H. Hui	3547 2133	3465 2899
Kong Ltd.)	IEC	F. C. Tsang	3547 2134	3465 2899
Contractor (Dragages – Bouygues Joint Venture)	Environmental Manager	C.F. Kwong	2293 7322	2293 7499
,	Environmental Officer	Bryan Lee	2293 7323	2293 7499
	24-hour complaint hotline	Rachel Lam	2293 7330	
ET (ERM-HK)	ET Leader	Jovy Tam	2271 3113	2723 5660

1.4 SUMMARY OF CONSTRUCTION WORKS

The construction phase of this Contract was commenced on 1 November 2013. The three-month rolling construction programme is shown in *Appendix B*.

With reference to DBJV's information, details of major construction works carried out in this reporting period are summarized in *Table 1.2*.

The general layout plan of the site showing the detailed works areas is shown in *Figure 1.2*. The Environmental Sensitive Receivers in the vicinity of the Project are shown in *Figure 1.3*.

The implementation schedule of environmental mitigation measures is presented in *Appendix C*.

Table 1.2 Summary of Construction Activities Undertaken during the Reporting Period

Construction Activities Undertaken

Land-based Works

Portion N-A

- Box Culvert Extension
- Startup of TBM
- Delivery & Assembly of TBM


Portion N-B


• TBM Tunnel Works

Portion N-C

- Surcharge Removal
- Excavation for Ventilation Shaft
- Set up of Slurry Treatment Plant
- Construction of capping beam and base slab for Ventilation Shaft
- Installation of Tower Crane
- Modification and Maintenance Works for Slurry Treatment Plant

Figure 1.2 Locations of Construction Activities – June 2015 to August 2015

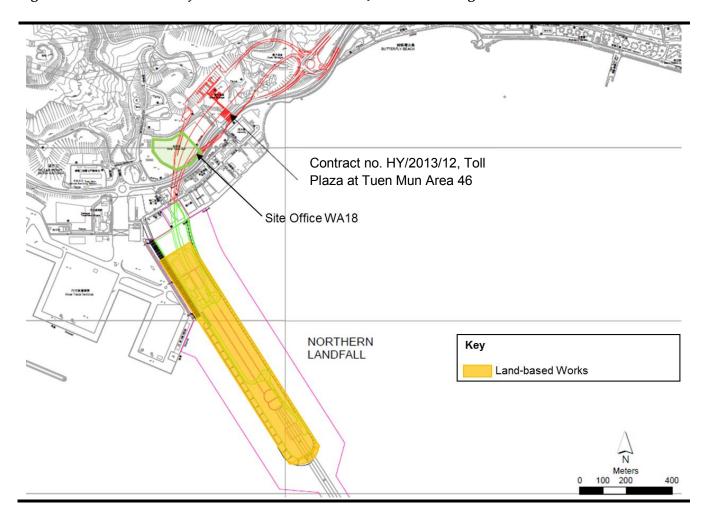

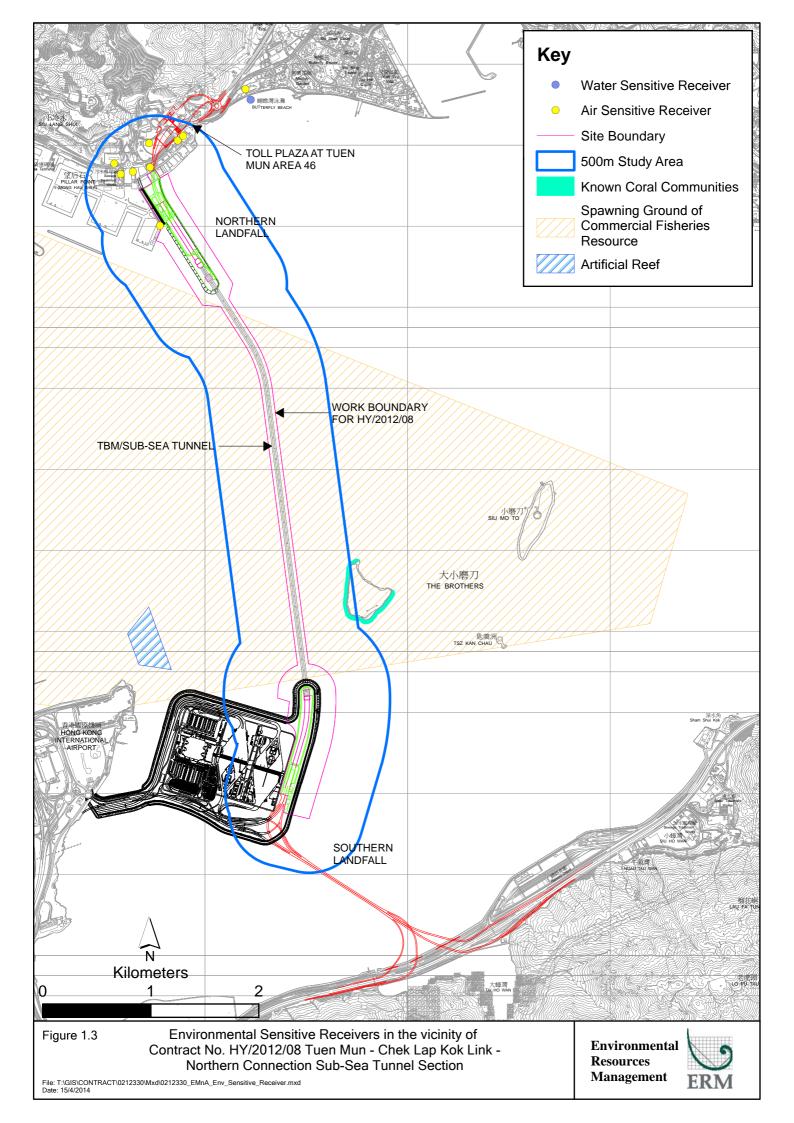

2 EM&A RESULTS

The EM&A programme required environmental monitoring for air quality, water quality and marine ecology as well as environmental site inspections for air quality, noise, water quality, waste management, marine ecology and landscape and visual impacts. The EM&A requirements and related findings for each component are summarized in the following sections

2.1 AIR QUALITY

As per the requirements under *Condition 2.4* of *EP-354/2009/D*, the Enhanced TSP Monitoring Plan has been prepared under *Contract No. HY/2012/08*. Details of the monitoring plan are presented in the *Enhanced TSP Monitoring Plan* (1).

2.1.1 Monitoring Requirements and Equipment

In accordance with the Updated EM&A Manual and the *Enhanced TSP Monitoring Plan*, impact 1-hour TSP monitoring was conducted three (3) times in every six (6) days and impact 24-hour TSP monitoring was carried out once in every six (6) days when the highest dust impact was expected. 1-hr and 24-hr TSP monitoring frequency was increased to three times per day every three days and daily every three days respectively as excavation works for launching shaft commenced on 24 October 2014.

High volume samplers (HVSs) were used to carry out the 1-hour and 24-hour TSP monitoring in the reporting quarter at the five (5) air quality monitoring stations in accordance with the requirements stipulated in the Updated EM&A Manual (*Figure 2.1*; *Table 2.1*). Wind anemometer was installed at the rooftop of ASR5 for logging wind speed and wind direction. Details of the equipment deployed are provided in *Table 2.2*.

ERM (2013) Enhanced TSP Monitoring Plan. Submitted on 28 October 2013 and subsequently approved by EPD on 1 November 2013.

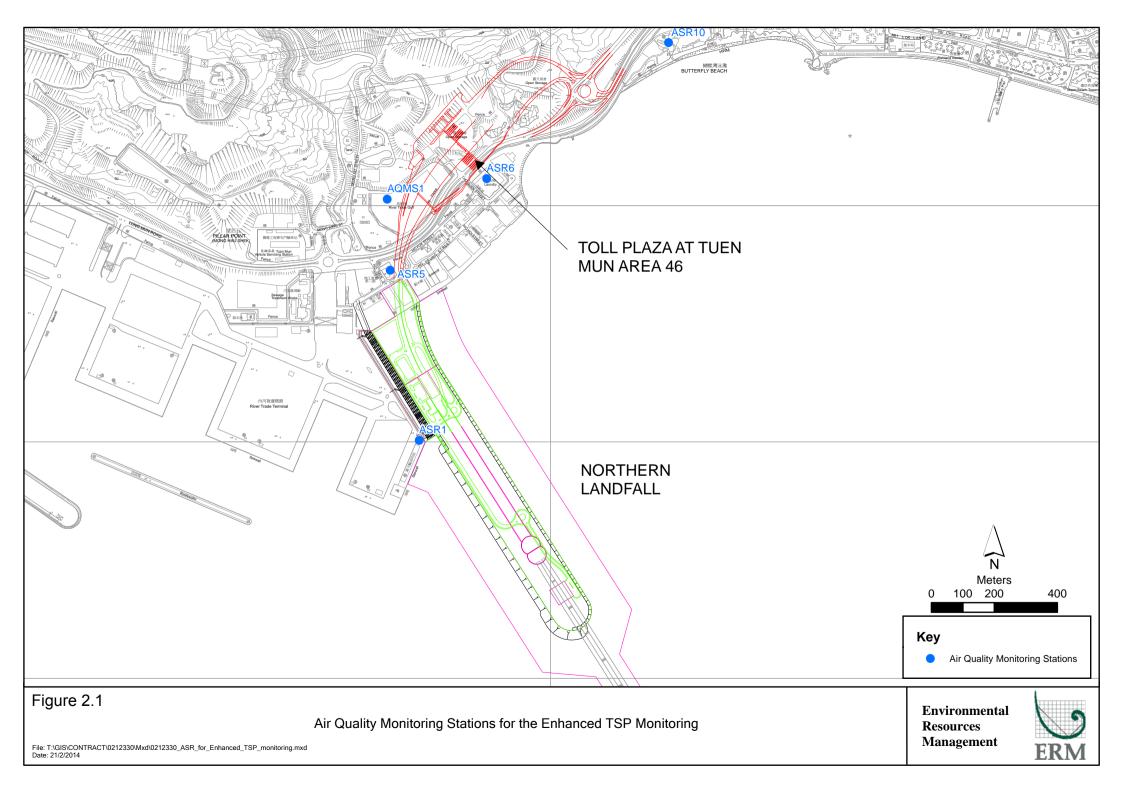


Table 2.1 Locations of Impact Air Quality Monitoring Stations and Monitoring Dates in this Reporting Period

Monitoring	Location	Description	Parameters & Frequency	Monitoring
Station			- •	Dates
ASR1	Tuen Mun	Office	TSP monitoring	2, 5, 8, 11, 14, 17,
	Fireboat Station		 1-hour Total Suspended 	20, 23, 26 and 29
ASR5	Pillar Point Fire	Office	Particulates (1-hour TSP,	June 2015;
	Station		$\mu g/m^3$), 3 times in every 6	2,5,7,10,13,
AQMS1	Previous River	Bare ground	days	16,19,22,25,
	Trade Golf		 24-hour Total Suspended 	28 and 31 July
ASR6	Butterfly Beach	Office	Particulates (24-hour TSP,	2015;
	Laundry		$\mu g/m^3$), daily for 24-hour	3, 6, 9, 12, 15, 18,
ASR10	Butterfly Beach	Recreational	in every 6 days	21, 24, 27 and 30
	Park	uses	Enhanced TSP monitoring	August 2015.
			(commenced on 24 October	
			2014)	
			 1-hour Total Suspended 	
			Particulates (1-hour TSP,	
			$\mu g/m^3$), 3 times in every 3	
			days	
			• 24-hour Total Suspended	
			Particulates (24-hour TSP,	
			$\mu g/m^3$), daily for 24-hour	
			in every 3 days	

Table 2.2 Air Quality Monitoring Equipment

Equipment	Brand and Model
High Volume Sampler (1-hour TSP and 24-hour TSP)	Tisch Environmental Mass Flow Controlled Total Suspended Particulate (TSP) High Volume Sampler (Model No. TE-5170)
Wind Meter	Davis (Model: Weather Wizard III (S/N: WE90911A30)
Wind Anemometer for calibration	Lutron (Model No. AM-4201)

2.1.2 Action & Limit Levels

The Action and Limit Levels of the air quality monitoring is provided in *Appendix D*. The Event and Action plan is presented in *Appendix I*.

2.1.3 Monitoring Schedule for the Reporting Quarter

The schedules for air quality monitoring in the reporting quarter are provided in *Appendix E*.

2.1.4 Results and Observations

Impact air quality monitoring was conducted at all designated monitoring stations in the reporting period under favourable weather conditions. The major dust sources in the reporting period include construction activities under the Contract as well as nearby traffic emissions.

The monitoring results for 1-hour TSP and 24-hour TSP are summarized in *Tables 2.3* and 2.4, respectively. Monitoring results are presented graphically in *Appendix F* and detailed impact air quality monitoring data were reported in the *Seventeenth* to *Nineteenth Monthly EM&A Report*.

Table 2.3 Summary of 1-hour TSP Monitoring Results in this Reporting Period

Month/Year	Station	Average (μg/m³)	Range (µg/m³)	Action Level (μg/m³)	Limit Level (µg/m³)
June 2015 to	ASR 1	95	48 - 214	331	500
August 2015	ASR 5	147	66 - 252	340	500
	AQMS1	92	49 - 165	335	500
	ASR6	128	53 - 235	338	500
	ASR10	73	46 - 143	337	500

Table 2.4 Summary of 24-hour TSP Monitoring Results in this Reporting Period

Month/Year	Station	Average (μg/m³)	Range (µg/m³)	Action Level (μg/m³)	Limit Level (µg/m³)
June 2015 to	ASR 1	60	42 - 94	213	260
August 2015	ASR 5	78	51 - 127	238	260
	AQMS1	59	45 - 86	213	260
	ASR6	69	45 - 103	238	260
	ASR10	53	41 - 86	214	260

No Action or Limit Level exceedances for 1-hr TSP were recorded. No Action or Limit Level exceedances for 24-hr TSP were recorded. Summary of Exceedances for Air Quality Impact Monitoring in this Reporting Quarter is detailed in *Table 2.15*.

2.2 WATER QUALITY MONITORING

The baseline water quality monitoring undertaken by the Hong Kong – Zhuhai – Macao Bridge Hong Kong Projects (HKZMB) between 6 and 31 October 2011 has included all monitoring stations for the Project. Thus, the baseline monitoring results and Action/Limit Levels presented in HKZMB Baseline Monitoring Report (1) are adopted for this Project.

2.2.1 Monitoring Requirements & Equipment

In accordance with the Updated EM&A Manual, impact water quality monitoring was carried out three days per week during the construction period at nine (9) water quality monitoring stations (*Figure 2.2; Table 2.5*).

Table 2.5 Locations of Water Quality Monitoring Stations and the Corresponding Monitoring Requirements

Station ID	Type	Coor	dinates	*Parameters, unit	Depth	Frequency
	•	Easting	Northing	-		
IS12	Impact Station	813218	823681	• Temperature(°C)	3 water depths: 1m	Impact
IS13	Impact Station	813667	824325	 pH(pH unit) 	below sea surface,	monitoring: 3
IS14	Impact Station	812592	824172	• Turbidity (NTU)	mid-depth and 1m	days per week,
IS15	Impact Station	813356	825008	• Water depth (m)	above sea bed. If	at mid-flood
CS4	Control / Far	810025	824004	 Salinity (ppt) 	the water depth is	and mid-ebb
	Field Station			 DO (mg/L and 	less than 3m, mid-	tides during the
CS6	Control / Far	817028	823992	% of	depth sampling	construction
	Field Station			saturation)	only. If water	period of the
SR8	Sensitive	816306	825715	 SS (mg/L) 	depth less than 6m,	Contract.
	receiver				mid-depth may be	
	(Gazettal				omitted.	
	beaches in					
	Tuen Mun)					
SR9	Sensitive	813601	825858			
	receiver					
	(Butterfly					
	Beach)					
SR10A	Sensitive	823741	823495			
	receiver					
	(Ma Wan					
	FCZ)					

^{*}Notes:

In addition to the parameters presented monitoring location/position, time, water depth, sampling depth, tidal stages, weather conditions and any special phenomena or works underway nearby were also recorded.

Table 2.6 summarizes the equipment used in the impact water quality monitoring programme.

⁽¹) Agreement No. CE 35/2011 (EP) Baseline Environmental Monitoring for Hong Kong - Zhuhai - Macao Bridge Hong Kong Projects - Investigation. Baseline Environmental Monitoring Report (Version C). Submitted on 8 March 2012 and subsequently approved by EPD.

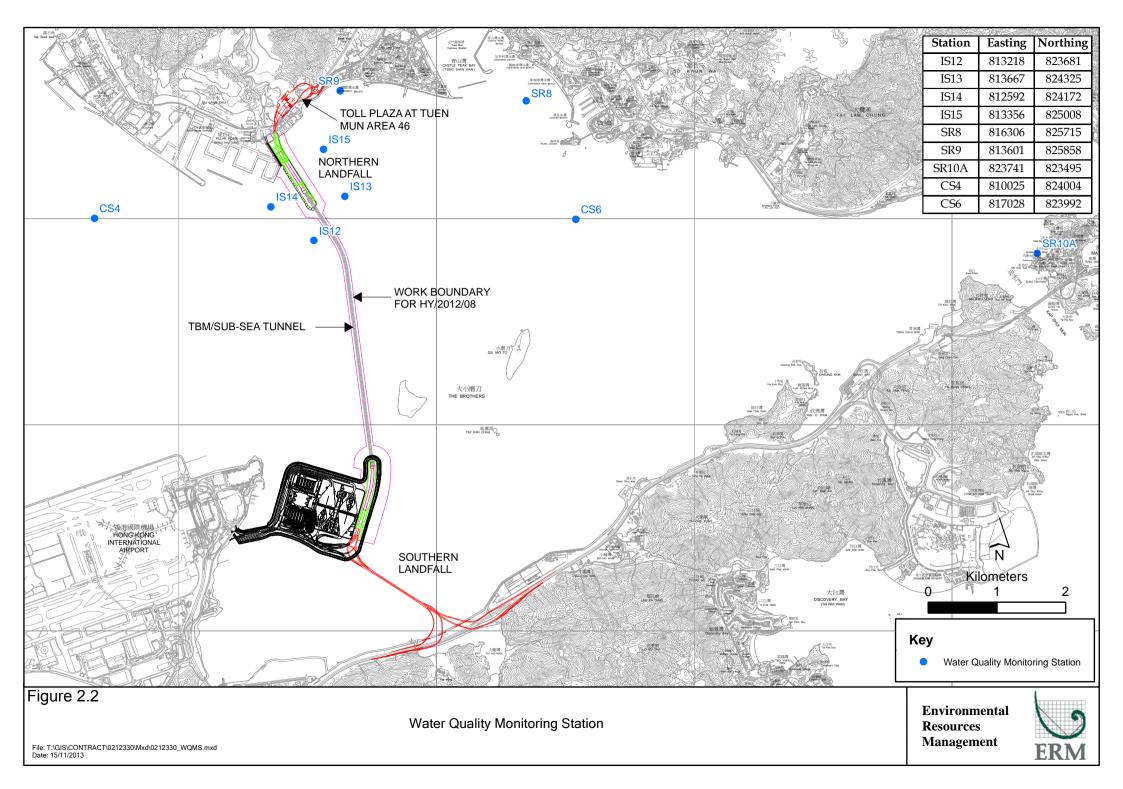


Table 2.6 Water Quality Monitoring Equipment

Equipment	Model	Qty.
Water Sampler	Kahlsico Water-Bottle Model 135DW 150	1
Dissolved Oxygen Meter	YSI Pro 2030	1
pH Meter	HANNA HI 8314	1
Turbidity Meter	HACH 2100Q	1
Monitoring Position	"Magellan" Handheld GPS Model eXplorist GC	4
Equipment	DGPS Koden KGP913MK2 (1)	1

2.2.2 Action & Limit Levels

The Action and Limit Levels of the water quality monitoring is provided in *Appendix D*. The Event and Action plan is presented in *Appendix I*.

2.2.3 Monitoring Schedule for the Reporting Period

The schedules for water quality monitoring in the reporting period are provided in *Appendix E*.

As informed by the Contractor, Phase I Reclamation works for the Northern Landfall was substantially completed in December 2014, a proposal letter was sent to EPD on 21 May 2015 to seek approval for the temporary suspension of Water Quality Monitoring. Subsequently, a letter from EPD on 5 June 2015 stated that they have no strong objection to the temporary suspension of the water quality monitoring. Water Quality Monitoring was suspended from 6 June 2015 effectively and will resume when Phase II Reclamation commences in the fourth quarter of 2016 tentatively.

2.2.4 Results and Observations

During this reporting period, no marine works was carried out in this Contract. It is useful to note that heavy marine traffic (not associated with the Project) was commonly observed nearby the Project site and its vicinity.

Impact water quality monitoring was conducted at all designated monitoring stations in the reporting period under favourable weather conditions. Monitoring results are presented graphically in *Appendix G* and detailed impact water quality monitoring data were reported in the *Twentieth Monthly EM&A Report*.

In this reporting period, a total of three monitoring events were undertaken in which no exceedances were recorded. Summary of Exceedances for Water Quality Impact Monitoring in this Reporting Quarter is detailed in *Table 2.17*.

2.3 DOLPHIN MONITORING

2.3.1 *Monitoring Requirements*

Impact dolphin monitoring is required to be conducted by a qualified dolphin specialist team to evaluate whether there have been any effects on the

dolphins. In order to fulfil the EM&A requirements and make good use of available resources, the on-going impact line transect dolphin monitoring data collected by HyD's *Contract No. HY/2011/03 Hong Kong-Zhuhai-Macao Bridge. Hong Kong Link Road - Section between Scenic Hill and Hong Kong Boundary Crossing Facilities* on the monthly basis is adopted to avoid duplicates of survey effort.

2.3.2 Monitoring Equipment

Table 2.7 summarises the equipment used for the impact dolphin monitoring.

Table 2.7 Dolphin Monitoring Equipment

Equipment	Model
Global Positioning System (GPS)	Garmin 18X-PC
	Geo One Phottix
Camera	Nikon D90 300m 2.8D fixed focus
	Nikon D90 20-300m zoom lens
Laser Binoculars	Infinitor LRF 1000
Marine Binocular	Bushell 7 x 50 marine binocular with compass
Vessel for Monitoring	and reticules
	65 foot single engine motor vessel with
	viewing platform 4.5m above water level
	~ ·


2.3.3 Monitoring Parameter, Frequencies & Duration

Dolphin monitoring should cover all transect lines in Northeast Lantau (NEL) and the Northwest Lantau (NWL) survey areas twice per month throughout the entire construction period. The monitoring data should be compatible with, and should be made available for, long-term studies of small cetacean ecology in Hong Kong. In order to provide a suitable long-term dataset for comparison, identical methodology and line transects employed in baseline dolphin monitoring was followed in the impact dolphin monitoring.

2.3.4 Monitoring Location

The impact dolphin monitoring was carried out in the NEL and NWL along the line transect as depicted in *Figure 2.3*. The co-ordinates of all transect lines are shown in *Table 2.8* below.

10

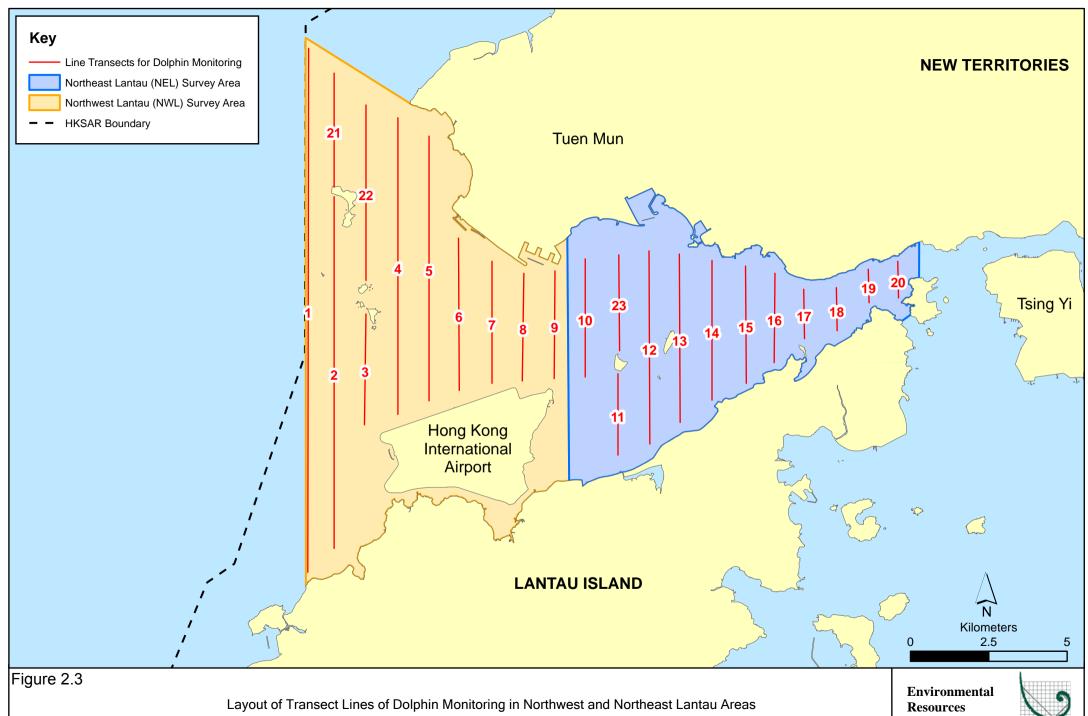

File: T:\GIS\CONTRACT\0212330\Mxd\0212330_Transect_of_Dolphin_Monitoring.mxd Date: 29/11/2013

Management



 Table 2.8
 Impact Dolphin Monitoring Line Transect Co-ordinates

	Line No.	Easting	Northing		Line No.	Easting	Northing
1	Start Point	804671	814577 (815456)	13	Start Point	816506	819480
1	End Point	804671	831404	13	End Point	816506	824859
2	Start Point	805475	815457 (815913)	14	Start Point	817537	820220
2	End Point	805477	826654	14	End Point	817537	824613
3	Start Point	806464	819435	15	Start Point	818568	820735
3	End Point	806464	822911	15	End Point	818568	824433
4	Start Point	807518	819771	16	Start Point	819532	821420
4	End Point	807518	829230	16	End Point	819532	824209
5	Start Point	808504	820220	17	Start Point	820451	822125
5	End Point	808504	828602	17	End Point	820451	823671
6	Start Point	809490	820466	18	Start Point	821504	822371
6	End Point	809490	825352	18	End Point	821504	823761
7	Start Point	810499	820690 (820880)	19	Start Point	822513	823268
7	End Point	810499	824613	19	End Point	822513	824321
8	Start Point	811508	820847 (821123)	20	Start Point	823477	823402
8	End Point	811508	824254	20	End Point	823477	824613
9	Start Point	812516	820892 (821303)	21	Start Point	805476	827081
9	End Point	812516	824254	21	End Point	805476	830562
10	Start Point	813525	820872	22	Start Point	806464	824033
10	End Point	813525	824657	22	End Point	806464	829598
11	Start Point	814556	818449 (818853)	23	Start Point	814559	821739
11	End Point	814556	820992	23	End Point	814559	824768
12	Start Point	815542	818807				
12	End Point	815542	824882				

Note:

Northing coordinates in bracket are the changed coordinates started from surveys of August 2015 due to obstruction of permanent structures associated with construction works other than this Project.

2.3.5 Action & Limit Levels

The Action and Limit levels of dolphin impact monitoring are shown in *Appendix D*. The Event and Action plan is presented in *Appendix I*.

2.3.6 Monitoring Schedule for the Reporting Period

The dolphin monitoring schedules for the reporting period are shown in *Appendix E*.

2.3.7 Results & Observations

A total of 900.64 km of survey effort was conducted, with 92.8% of the total survey effort being conducted under favourable weather conditions (ie Beaufort Sea State 3 or below with good visibility) in this reporting quarter. Amongst the two areas, 345.58 km and 555.06 km of survey effort were conducted from NEL and NWL survey areas, respectively. The total survey effort conducted on primary and secondary lines were 655.74 km and 244.90 km, respectively. The survey efforts are summarized in *Appendix H*.

A total of 12 groups of 42 Chinese White Dolphin sightings were recorded during the six sets of surveys in this reporting quarter. All dolphin sightings were made during on-effort search. All on-effort sightings were made on primary lines. None of the dolphin groups was associated with operating fishing vessel. During this reporting quarter, eleven dolphin groups were sighted in NWL, while one dolphin group were sighted in NEL.

Encounter rates of Chinese White Dolphins are deduced from the survey effort and on-effort sighting data made under favourable conditions (Beaufort 3 or below with good visibility) in the reporting quarter with the results and comparison with baseline results present in *Tables 2.9* and *2.10*.

Table 2.9 Individual Survey Event Encounter Rates

		Encounter rate (STG)	Encounter rate (ANI)
		(no. of on-effort dolphin	(no. of dolphins from all on-
		sightings per 100 km of	effort sightings per 100 km of
		survey effort)	survey effort)
		Primary Lines Only	Primary Lines Only
	Set 1: Jun 2 nd /10 th	0.0	0.0
	Set 2: Jun 24th/26th	2.64	2.64
NEL	Set 3: Jul 2 nd /7 th	0.0	0.0
NEL	Set 4: Jul 22 nd / 27 th	0.0	0.0
	Set 5: Aug 10th/14th	0.0	0.0
	Set 6: Aug 19th/28th	0.0	0.0
	Set 1: Jun 2 nd /10 th	1.51	15.15
	Set 2: Jun 24th/26th	0.0	0.0
NWL	Set 3: Jul 2 nd /7 th	1.69	3.38
INVVL	Set 4: Jul 22 nd / 27 th	3.46	6.92
	Set 5: Aug 10th/14th	0.0	0.0
	Set 6: Aug 19th/28th	8.53	29.84

Note: Dolphin Encounter Rates are deduced from the Two Sets of Surveys (Two Surveys in Each Set) in the reporting quarter in Northeast (NEL) and Northwest Lantau (NWL)

Table 2.10 Quarterly Average Encounter Rates

	(no. of on-effort o	rate (STG) dolphin sightings survey effort)	Encounter rate (ANI) (no. of dolphins from all on-effort sightings per 100 km of survey effort)		
	June 2015 – August 2015	September 2011 - November 2011	June 2015 – August 2015	September 2011 - November 2011	
Northeast Lantau	0.44 ± 1.08	6.00 ± 5.05	0.44 ± 1.08	22.19 ± 26.81	
Northwest Lantau	2.53 ± 3.20	9.85 ± 5.85	9.21 ± 11.57	44.66 ± 29.85	

Note: Encounter rates deduced from the baseline monitoring period have been recalculated based only on survey effort and on-effort sighting data made along the primary transect lines under favourable conditions.

Group size of Chinese White Dolphins ranged from 1 - 10 individuals per group in North Lantau region during June 2015 to August 2015. The average dolphin group sizes from these three months were compared with the ones deduced from the baseline period in September to November 2011, as shown in *Table 2.11*.

Table 2.11 Average Dolphin Group Size

	Average Dolphin Group Size							
	June 2015 – August 2015 September 2011 – Novemb							
Overall	3.50 ± 2.65 3.72 ± 3.13							
Northeast Lantau	1.0	3.18 ± 2.16						
Northwest Lantau	3.73 ± 2.65	3.92 ± 3.40						

Whilst one Limit Level exceedance was observed for the quarterly dolphin monitoring data between June 2015 and August 2015, no unacceptable impact from the construction activities of this Contract was recorded from the general observations.

Although the dolphins infrequently occurred along the alignment of TM-CLKL Northern Connection Sub-Sea Tunnel Section in the past and during the baseline monitoring period, it is apparent that dolphin usage has been significantly reduced in NEL.

It is critical to monitor the dolphin usage in North Lantau region in the upcoming quarters to determine whether the dolphins are continuously affected by the various construction activities in relation to the HZMB-related works, and whether suitable mitigation measure can be applied to revert the situation.

2.3.8 Implementation of Marine Mammal Exclusion Zone

There was no dredging, reclamation or marine sheet piling works in open waters during this reporting period. Thus, Passive Acoustic Monitoring (PAM) and the day-time monitoring of Dolphin Exclusion Zone (DEZ) by dolphin observers were not in effect during the reporting period.

2.4 EM&A SITE INSPECTION

Site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures under the Contract. Thirteen (13) site inspections were carried out in the reporting quarter on 3, 10, 17 and 24 June 2015; 2, 8, 15, 22 and 29 July 2015; 6, 12, 19 and 26 August 2015.

Key observations during the site inspections in this reporting period are summarized in *Table 2.12*.

Table 2.12 Specific Observations and Recommendations during the Weekly Site Inspection in this Reporting Period

Inspection Date	Environmental Observations	Recommendations/ Remarks
3 June 2015	 Works Area - Portion N-A Bund for the chemical container should be maintained with sufficient capacity. Chemical container should be stored in chemical storage area. 	 Works Area - Portion N-A The Contractor was reminded to provide bund with sufficient capacity for the chemical container. The Contractor was reminded to store the chemical container in chemical storage area.
10 June 2015	 Works Area - Portion N-B Accumulated general refuse was observed on the ground. Chemical spillage should be cleaned up and disposed as chemical waste. Excess materials should be cleaned up for maintenance of the soak-away pit. 	 Works Area - Portion N-B The Contractor was reminded to provide trays for the accumulated general refuse. The Contractor was reminded to clean up the chemical spillage disposed as chemical waste. The Contractor was reminded to clean up the excess materials for the soakaway pit.
17 June 2015	 Works Area - Portion N-A Drip tray should be regularly maintained. Chemical label and drip tray should be provided to the oil drum. 	 Works Area - Portion N-A The Contractor was reminded to check and maintain drip tray regularly. The Contractor was reminded to provide the chemical label and drip tray to the oil drum.
24 June 2015	 Works Area - Portion N-A Chemical label and drip tray should be provided to the oil drum. Excess muddy water should be cleared. Chemical labels and drip tray should be provided to the oil drums. 	 Works Area - Portion N-A The Contractor was reminded to provide chemical label and drip tray for the oil drum. The Contractor was reminded to clear the excess muddy water. The Contractor was reminded to provide chemical labels and drip tray for the oil drums.
2 July 2015	 Works Area - Portion N-B Site drainage should be maintained more frequently. Chemical containers should be placed in chemical storage area. 	 Works Area - Portion N-A The Contractor was reminded to regularly check and maintain the capacity of site drainage. The Contractor was reminded to place the chemical containers in the chemical storage area while not in use.
8 July 2015	 Works Area - Portion N-A Chemical labels should be provided to the chemical containers. Accumulated general refuse should be cleared. Chemical container should be placed in chemical storage area and chemical labels should be provided. 	 Works Area - Portion N-A The Contractor was reminded to provide chemical labels to the chemical containers. The Contractor was reminded to clear accumulated general refuse. The Contractor was reminded to place the chemical container in chemical storage area and provide chemical label to the chemical container.
15 July 2015	 Works Area - Portion N-A Accumulated general refuse should be cleared more frequently. Works Area - Portion N-B Excess sandy material should be cleared more 	 Works Area - Portion N-A The Contractor was reminded to clear the accumulated general refuse. Works Area - Portion N-B The Contractor was reminded to clear

Inspection Date	Environmental Observations	Recommendations/ Remarks
22 July 2015	 Works Area - Portion N-A Accumulated general refuse should be cleared more frequently. Drip tray should be clear of sandy materials. Excess sandy materials should be cleared to maintain capacity of the silt removal facilities. 	 Works Area - Portion N-A The Contractor was reminded to clear the accumulated general refuse. The Contractor was reminded to clear the sandy materials in the drip tray. The Contractor was reminded to place clear the excess sandy materials in the silt removal facilities.
29 July 2015	 Works Area - Portion N-A Excess sandy materials should be cleared to avoid runoff. Works Area - Portion N-B Muddy water should be cleared to avoid runoff. Watering should be applied to the materials during loading of barges. 	 Works Area - Portion N-A The Contractor is reminded to clear the excess sandy materials to avoid runoff. Works Area - Portion N-B The Contractor is reminded to clear the muddy water to avoid runoff. The Contractor is reminded to apply watering to the materials during loading of barges.
6 August 2015	 Works Area - Portion N-A Floating litter adjacent to the work site should be cleared more frequently. Water spraying should be applied more frequently during windy condition. 	 Works Area - Portion N-A The Contractor was reminded to check and clear the floating litter more frequently. The Contractor was reminded to provide water spraying more frequently during windy condition.
12 August 2015	 Works Area - Portion N-A Drip tray and chemical label should be provided to the oil drum. Works Area - Portion N-B Water inside drip tray should be cleared after rainstorm. Excess sandy materials should be cleared. Works Area - Portion N-C Accumulated general refuse should be cleared. Muddy water should be cleared to avoid runoff. 	 Works Area - Portion N-A The Contractor was reminded to provide drip tray and chemical label to the oil drum. Works Area - Portion N-B The Contractor was reminded to check and clear the water inside drip tray after rainstorm. The Contractor was reminded to clear the excess sandy materials more frequently. Works Area - Portion N-C The Contractor was reminded to clear the accumulated general refuse more frequently. The Contractor was reminded to clear the accumulated general refuse more frequently. The Contractor was reminded to clear the muddy water avoid runoff.
19 August 2015	 Works Area - Portion N-A Water inside drip tray should be cleared after rainstorm to maintain capacity. Excess muddy materials should be cleared more frequently. Used chemical containers should be cleared or placed inside of drip trays. Accumulated general refuse should be cleared. 	 Works Area - Portion N-A The Contractor was reminded to check the capacity of drip trays more frequently. The Contractor was reminded to clear the excess muddy more frequently. The Contractor was reminded to clear the used chemical containers or placed them inside of drip trays. The Contractor was reminded to clear the accumulated general refuse.

Inspection Date	Environmental Observations	Recommendations/ Remarks
26 August 2015	 Works Area - Portion N-A Wetsep should be kept in adequate capacity to avoid any overflow. Trays for general refuse should be provided. Works Area - Portion N-C Materials other than chemical containers 	Works Area - Portion N-A The Contractor was reminded to maintain adequate capacity of the wetsep to avoid any overflow. The Contractor was reminded to provide trays for general refuse.
	 should be seperated from the drip tray. Deposited silt should be removed in the channel. 	 Works Area - Portion N-C The Contractor was reminded to clear the materials other than chemical containers in the drip tray. The Contractor was reminded to remove the deposited silt in the channel.

The Contractor has rectified all of the observations as identified during environmental site inspections in the reporting quarter.

2.5 WASTE MANAGEMENT STATUS

The Contractor had submitted application form for registration as chemical waste producer under the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.

Wastes generated during this reporting period include mainly construction wastes (inert and non-inert) and imported fill. Reference has been made to the waste flow table prepared by the Contractor (*Appendix K*). The quantities of different types of wastes are summarized in *Table 2.13*.

Table 2.13 Quantities of Different Waste Generated in the Reporting Period

Month/Year	Inert	Imported	Inert	Non-inert	Recyclable	Chemical	Marine Sec	diment (m³)
	Construction Waste (a) (tonnes)	Fill (tonnes)	Construction Waste Re- used	Construction Waste (b) (tonnes)	Materials (c) (kg)	Wastes (kg)	Category L	Category M
			(tonnes)					
June 2015	247,282	0	0	120	0	0	0	0
July 2015	233,422	0	0	172	0	0	0	0
August 2015	62,367	0	0	246	300	0	0	0
Total	543,071	0	0	538	300	0	0	0

Notes:

- (a) Inert construction wastes include hard rock and large broken concrete, and materials disposed as public fill.
- (b) Non-inert construction wastes include general refuse disposed at landfill.
- (c) Recyclable materials include metals, paper, cardboard, plastics, timber and others.

The Contractor was advised to properly maintain on site C&D materials and waste collection, sorting and recording system, dispose of C&D materials and wastes at designated ground and maximize reuse/ recycle of C&D materials and wastes. The Contractor was also reminded to properly maintain the site tidiness and dispose of the wastes accumulated on site regularly and properly.

For chemical waste containers, the Contractor was reminded to treat properly and store temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.

2.6 ENVIRONMENTAL LICENSES AND PERMITS

The status of environmental licensing and permit is summarized in $\it Table~2.14$ below.

Table 2.14 Summary of Environmental Licensing and Permit Status

License/ Permit	License or Permit No.	Date of Issue	Date of Expiry	License/ Permit	Remarks
				Holder	
Environmental Permit	EP-354/2009/D	13 March 2015	Throughout the	HyD	Application for VEP on 3 March 2015 to
			Contract		supersede EP-354/2009/C
Construction Dust Notification	363510	19 August 2013	Throughout the	DBJV	-
			Contract		
Chemical Waste Registration	5213-422-D2516-01	10 September 2013	Throughout the	DBJV	-
			Contract		
Construction Waste Disposal	7018108	19 August 2013	Throughout the	DBJV	Waste disposal in Contract HY/2012/08
Account			Contract		
Waste Water Discharge License	WT00017707-2013	18 November 2013	30 November 2018	DBJV	For works in site WA18
Waste Water Discharge License	WT00019248-2014	5 June 2014	30 June 2019	DBJV	For site Portion N6 and Reclamation
					Area E
Construction Noise Permit	GW-RW0140-15	29 March 2015	28 September 2015	DBJV	For Portion N6
Construction Noise Permit	GW-RW0150-15	1 April 2015	30 September 2015	DBJV	For GI Works at Southern Landfall
Construction Noise Permit	GW-RW0204-15	11 May 2015	10 November 2015	DBJV	For site WA23
Construction Noise Permit	GW-RW0350-15	14 July 2015	13 December 2015	DBJV	For site WA23
Construction Noise Permit	GW-RW0216-15	20 May 2015	19 July 2015	DBJV	For Dredging and Reclamation Works
Construction Noise Permit	GW-RW0311-15	20 July 2015	19 October 2015	DBJV	For Dredging and Reclamation Works

Notes:

HyD = Highways Department

DBJV = Dragages - Bouygues Joint Venture

VEP = Variation of Environmental Permit

2.7 IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

In response to the site audit findings, the Contractors carried out all corrective actions.

A summary of the Implementation Schedule of Environmental Mitigation Measures (EMIS) is presented in *Appendix C*. The necessary mitigation measures relevant to this Contract were implemented properly.

2.8 SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMANCE LIMIT

For air quality impact monitoring, a total of thirty-one monitoring events were undertaken in which no Action Level or Limit Level exceedances for 1-hr TSP; no Action Level exceedances or Limit Level exceedances for 24-hr TSP were recorded in this reporting quarter. (*Table 2.15*).

Table 2.15 Summary of Exceedances for Air Quality Impact Monitoring in this Reporting Quarter

Station	Exceedance Level	Date of E	xceedances	Number of	Exceedances
		1-hr TSP	24-hr TSP	1-hr TSP	24-hr TSP
AQMS1	Action Level	-	-	0	0
	Limit Level	-	-	0	0
ASR1	Action Level	-	-	0	0
	Limit Level	-	-	0	0
ASR5	Action Level	-	-	0	0
	Limit Level	-	-	0	0
ASR6	Action Level	-	-	0	0
	Limit Level	-	-	0	0
ASR10	Action Level	-	-	0	0
	Limit Level	-	-	0	0
	Total number of A	Action level	Exceedances:	0	0
	Total number of	Exceedances:	0	0	

For marine water quality impact monitoring, a total of three monitoring events were undertaken in which no exceedances were recorded (*Table 2.16*).

Table 2.16 Summary of Exceedances for Marine Water Quality Impact Monitoring in this Reporting Quarter

Station	Exceedance Level (a) —	DO (Surface	and Middle)	DO (Bottom)	Turbidity (d	epth-averaged)	SS (depth	-averaged)
Station	Exceedance Level (a) —	Mid-ebb	Mid-flood	Mid-ebb	Mid-flood	Mid-ebb	Mid-flood	Mid-ebb	Mid-flood
004	AL	-	-	-	-	-	-	-	-
CS4	LL	-	-	-	-	-	-	-	-
CCC	\mathbf{AL}	-	-	-	-	-	-	-	-
CS6	LL	-	-	-	-	-	-	-	-
1010	\mathbf{AL}	-	-	-	-	-	-	-	-
IS12	LL	-	-	-	-	-	-	-	-
1010	\mathbf{AL}	-	-	-	-	-	-	-	-
IS13	LL	-	-	-	-	-	-	-	-
AL AL	\mathbf{AL}	-	-	-	-	-	-	-	-
IS14	LL	-	-	-	-	-	-	-	-
IC1E	\mathbf{AL}	-	-	-	-	-	-	-	-
IS15	LL	-	-	-	-	-	-	-	-
CDO AL	\mathbf{AL}	-	-	-	-	-	-	-	-
SR8	LL	-	-	-	-	-	-	-	-
CDO	\mathbf{AL}	-	-	-	-	-	-	-	_
SR9	LL	-	-	-	-	-	-	_	_
CD40	\mathbf{AL}	-	-	-	-	-	-	_	_
SR10	LL	_	_	-	-	-	-	_	_
	Total AL Exceedances:	0	0	0	0	0	0	0	0
	Total LL Exceedances:	0	0	0	0	0	0	0	0

Notes:

(a) AL = Action Level; LL = Limit Level

One Limit Level exceedance of impact dolphin monitoring was recorded in this reporting quarter. Following the review of monitoring data and marine works details in accordance with the procedures stipulated in the Event and Action Plan of the Updated EM&A Manual, there is no evidence showing that the sources of impact directly related to the construction works under this Contract that may have affected the dolphin usage in the NEL region. Detailed investigation findings are presented in *Appendix J*.

Cumulative statistics are provided in *Appendix J*.

2.9 SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS


The Environmental Complaint Handling Procedure is provided in *Figure 2.4*.

No non-compliance event was recorded during the reporting period.

No environmental complaint was received in the reporting period.

No summons/ prosecution was received during the reporting period.

Statistics on complaints, notifications of summons and successful prosecutions are summarized in *Appendix J*.

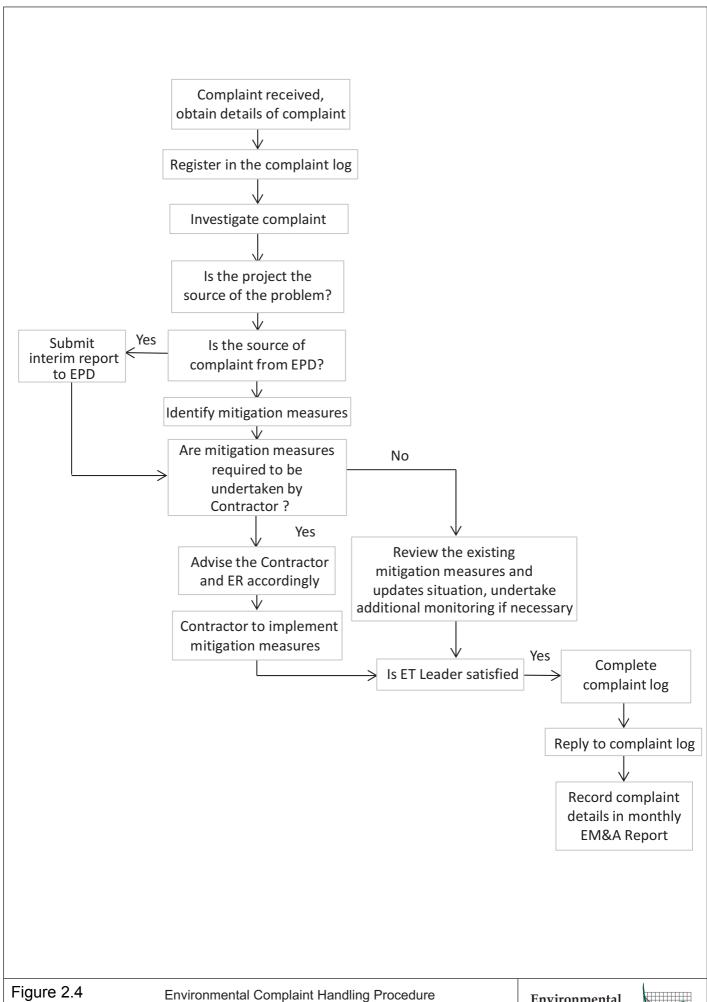

Environmental Resources Management



3 FUTURE KEY ISSUES

3.1 CONSTRUCTION ACTIVITIES FOR THE COMING QUARTER

As informed by the Contractor, the major works for the Project in the coming quarter are summarized in *Table 3.1*.

Table 3.1 Construction Works to Be Undertaken in the Coming Quarter

Works to be undertaken

Land-based Works

- Box Culvert Extension at Works Area Portion N-A;
- Installation of Tower Crane at Works Area Portion N-C;
- Base Slab Construction for Ventilation Shaft at Works Area Portion N-C;
- TBM Tunnel Works at Works Area Portion N-B; and
- Modification and Maintenance Works for Slurry Treatment Plant at Works Area Portion N-C.

3.2 KEY ISSUES FOR THE COMING QUARTER

Potential environmental impacts arising from the above upcoming construction activities are mainly associated with dust, marine ecology and waste management issues.

As informed by the Contractor, Phase I Reclamation works for the Northern Landfall was substantially completed in December 2014, a proposal letter was sent to EPD on 21 May 2015 to seek approval for the temporary suspension of Water Quality Monitoring. Subsequently, a letter from EPD on 5 June 2015 stated that they have no strong objection to the temporary suspension of the water quality monitoring. Water Quality Monitoring was suspended from 6 June 2015 effectively and will resume when Phase II Reclamation commences in the fourth quarter of 2016 tentatively.

3.3 MONITORING SCHEDULE FOR THE COMING QUARTER

Impact monitoring for air quality, marine water quality and marine ecology (include dolphin monitoring) are scheduled to continue for the next reporting period.

The monitoring programme has been reviewed and was considered as adequate to cater for the nature of works in progress. Change to the monitoring programme was thus not considered to be necessary at this stage. The monitoring programme will be evaluated as appropriate in the next reporting period.

4 CONCLUSIONS

This Seventh Quarterly EM&A Report presents the findings of the EM&A activities undertaken during the period from 1 June 2015 to 31 August 2015, in accordance with the Updated EM&A Manual and the requirements of *EP*-354/2009/D.

Air quality (including 1-hour TSP and 24-hour TSP), marine water quality and dolphin monitoring were carried out in the reporting period. No Action or Limit Level exceedances for 1-hr TSP were recorded. No Action or Limit Level exceedances for 24-hr TSP were record. No Action Level or Limit Level exceedances were recorded in marine water quality impact monitoring during the reporting period.

A total of 12 groups of 42 Chinese White Dolphin sightings were recorded during the six sets of surveys from June 2015 to August 2015. Whilst one Limit Level exceedance was recorded for the quarterly dolphin monitoring data between June 2015 and August 2015, no unacceptable impact from the construction activities of the TM-CLKL Northern Connection Sub-sea Tunnel Section on Chinese White Dolphins was noticeable from general observations. Although the dolphins infrequently occurred along the alignment of TM-CLKL Northern Connection Sub-Sea Tunnel Section in the past and during the baseline monitoring period, it is apparent that dolphin usage has been significantly reduced in NEL. It is critical to monitor the dolphin usage in North Lantau region in the upcoming quarters, to determine whether the dolphins are continuously affected by the various construction activities in relation to the construction works of the Contract, and whether suitable mitigation measure can be applied to improve the situation.

Thirteen weekly environmental site inspections were carried out in the reporting period. Recommendations on remedial actions provided for the deficiencies identified during the site audits were properly implemented by the Contractor. No non-compliance event was recorded during the reporting period.


No environmental complaint was received during the reporting period.

No summons/ prosecution was received during the reporting period.

The monitoring programme has been reviewed and was considered as adequate to cater for the nature of works in progress. Change to the monitoring programme was thus not recommended at this stage. The monitoring programme will be evaluated as appropriate in the next reporting period. The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Appendix A

Project Organization for Environmental Works

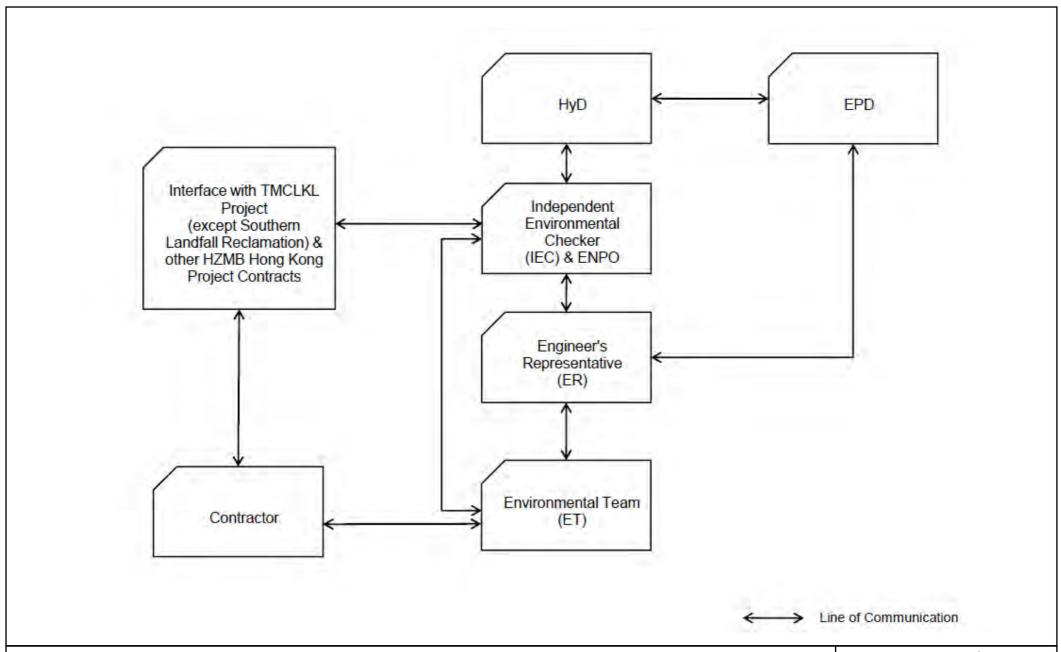

Appendix A1

Contract No. HY/2012/08 Northern Connection Sub-sea Tunnel Section Project Organization


Environmental Resources Management




Appendix B


Construction Programme


ctivity ID	Activity Name		Or Di		Planned Finish	Current Start	Current Finish	2015 201
			Di	JI Start	FIIIISII		FILIISH	May Jun Jul Aug Sep Oct Nov Dec Ja
TMCLK - Nortl General Subm		on Sub-Sea Tunnel Section						
	gn Submissions							
(A19) DDA for	Roadworks & Pro							
DD68370	SO's Review		3:	5 18-Sep-14	22-Oct-14	22-Dec-14A	15-Jul-15A	
(G6) IFA for Tu	unnel GBP SO's Review		3	5 29-Apr-14	02-Jun-14	03-Jul-14A	30-Aug-15	
DD70760	SO Approval with Condition	on R eceived	C		03-Jun-14		31-Aug-15	
Construction	Supervision Plan							
GEO1115	2nd GEO Review		2	3 29-Mar-14	25-Apr-14	01-Feb-14A	11-Jun-15 A	
Construction								
Northern Lan								
Construction	nation (Phase 1)							
Zone D1								
Reclamation NRC15160		ne D1 - (CH205 to 255) to +6mPD	1 8	09-Nov-15	5 17-Nov-15	17-Dec-15	19-Dec-15	Surcharge Removal
NRC15180		ne D1 - (CH255 to 305) to +6mPD	7			19-Dec-15A	07-Jan-16	Surcharge Ren
NRC15190	Surcharge Period - Zone I	D1 - (CH305 to 355)	18	0 19-Nov-14	17-May-15	03-Jun-15A	06-Jul-15A	Surcharge Period - Zone D1 - (CH3e5 to 355)
NRC15200	Surcharge Removal - Zor	ne D1 - (CH305 to 355)	7	18-May-15	5 26-May-15	03-Jun-15A	06-Jul-15A	Surchargel Removal - Zone D1 - (CH305 to 355)
Zone D2								
Reclamatio		DO (QUOES) (QE)		0 25 -		ament of the	amata in i	
	Surcharge Period - Zone I	· · · · · · · · · · · · · · · · · · ·	18			17-Nov-14A	15-May-15A	Surcharge Period - Zone D2 - (CH355 to 405)
NRC15220 NRC15230	Surcharge Removal - Zor Surcharge Period - Zone I		18			15-Jun-15A 21-Nov-14A	08-Jul-15A 19-May-15A	Surcharge Removal - Zone D2 - (CH355 to 405)
NRC15230 NRC15240	Surcharge Removal - Zone I		9			15-Jun-15A	19-May-15A 10-Jul-15A	Surcharge Period - Zone DZ - (CH405 to 443) Surcharge flemoval - Zone D2 - (CH405 to 443)
Zone C1	201 - 201	\		ii-oair is		.5 64.167	.5 00.107	Durona go monova - Euro DZ - (OT1400 IO 440)
Reclamation	on							
NRC15260	Surcharge Removal - Zor	ne C1 - (CH443 to 493)	11	06-May-17	7 17-May-17	27-Jun-15A	07-Aug-15A	
NRC15270	Surcharge Period - Zone (C1 - (CH493 to 543)	18	0 13-Nov-14	12-May-15	31-Dec-14A	28-Jun-15A	Surcharge Period - Zone C1 - (CH490 to 543)
NRC15280	Surcharge Removal - Zor	ne C1 - (CH493 to 543)	11	06-May-17	7 17-May-17	22-Jul-15A	14-Aug-15A	
Zone C2								
Reclamation NRC15290	Surcharge Period - Zone 0	C2 - (CH543 to 598)	18	0 05-Nov-14	03-May-15	31-Dec-14A	28-Jun-15A	Surcharge Period - Zone C2 - (CH543 to 598)
Zone B								
Vertical Sea								
	·	ng - Zone B - (CH598 to 648)	8			21-Oct-14A	16-Jul-15A	
NRC11410 NRC11420	·	ng - Zone B - (CH648 to 698) ng - Zone B - (CH698 to 738)	3	· ·		20-Nov-14A	16-Jul-15A	
	·	ng - Zone B - (Choss to 738)	6	20-Sep-14	29-Sep-14	02-Dec-14A	16-Jul-15A	
Reclamation NRC11990	Public Fill - Zone B - (CH	598 to 648) to +10mPD	ϵ	29-Aug-15	5 04-Sep-15	20-Sep-14A	22-Sep-14A	Public Fill - Zone B - (CH598/to 648) to +10mPl
NRC15310	Surcharge Period - Zone I	B - (CH598 to 648)	18	0 05-Sep-15	5 02-Mar-16	22-Sep-14A	20-Mar-15A	
NRC15320	Surcharge Removal - Zor	ne B - (CH598 to 648)	11	03-Mar-16	6 14-Mar-16	29-Aug-15	09-Sep-15	
NRC15360	Surcharge Removal - Zor	ne B - (CH698 to 738)	11	25-Mar-15	5 10-Apr-15	29-Aug-15	09-Sep-15	harge Removal - Zone B - (CH698 to 738)
Zone A1								
Reclamatio		20 A 1 (CH700 to 700)	-11	06 May 45	5 06-Jun-15	16-Jul-15A	16-Jul-15A	
	Surcharge Removal - Zor	IBA 1 - (CIT/36 to 793)	11	26-May-15	06-Jun-15	16-Jul-15A	16-Jul- 15A	Surcharge Removal - Zano V1 - (CH738 to 793)
Zone A2 Sloping Se	eawall							
	SS - Armour Rock - Zone	A2 - (CH843 to 893)	4	14-Jun-14	19-Jun-14	16-Apr-15A	29-Aug-15	
NRC12770	SS - Armour Rock - Zone	A2 - (CH893 to 956)	4	19-Jun-14	24-Jun-14	16-Apr-15A	31-Aug-15	
Reclamation		AC (CUITO) - 040)	46	10.5	00.145	44.14	00.1445.1	
	Surcharge Period - Zone A		18			11-Nov-14 A	09-May-15A	Surcharge Period - Zon - AG (CH793 to 843)
NRC15400	Surcharge Removal - Zor	10 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	11) 08-Jun-15	19-Jun-15	08-Jun-15A	02-Sep-15	Surcharge Removal - Zone A2 - (CH738 to 956)
Zone F CH184 to 0	CH231							
	F - Anchor wall Installation	n - CH184 to CH231	4	10-Feb-14	13-Feb-14	29-Aug-15	02-Sep-15	
A6416290	F - Backfilling up to 0.0m F	PD & G2 Installation to Anchor Wall- CH184 to CH231	1 3	14-Feb-14	16-Feb-14	16-Mar-15A	04-Sep-15	
A6416295	F - Backfilling up to +3.0m	nPD & G1 Installation to Anchor Wall- CH184 to CH2	31 2	17-Feb-14	18-Feb-14	16-Mar-15A	05-Sep-15	
		nPD to Anchor Wall - CH184 to CH231	2			06-Sep-15	07-Sep-15	
	-	O to Existing Seawall - CH184 to CH231	1	21-Feb-14	21-Feb-14	08-Sep-15	08-Sep-15	
CH231 to C A6416280	CH278 F - Backfilling up to +6.0m	nPD - CH231 to CH278	2	17- A pr-14	18-Apr-14	03-Sep-15	04-Sep-15	
	F - Anchor wall Installation		4	· ·		05-Sep-15	09-Sep-15	
		PD & G2 Installation to Anchor Wall- CH231 to CH278		· ·		03-Mar-15A	10-Sep-15	
A6416490		nPD & G1 Installation to Anchor Wall - CH231 to CH2				10-Mar-15A	11-Sep-15	
A6416500		nPD to Anchor Wall - CH231 to CH278	2	· ·		12-Sep-15	13-Sep-15	
A6416510		O to Existing Seawall - CH231 to CH278	1	03-May-14		14-Sep-15	14-Sep-15	
CH278 to C	CH327							
	F - Backfilling up to +6.0m	nPD - CH278 to CH327	2	12-Apr-14	13-Apr-14	01-Sep-15	02-Sep-15	
A6416340	F - Anchor wall Installation	n - CH278 to CH327	4	26-Apr-14	30-Apr-14	10-Sep-15	14-Sep-15	
	Ť .	PD & G2 Installation to Anchor Wall - CH278 to CH32		,		03-Mar-15A 10-Mar-15A	15-Sep-15 16-Sep-15	
age 1 of 12 roject ID: TMCLK_D rata Date: 28-Aug-15		Planned Bar Planned Bar - Critical Planned Milestone Progress bar Progress Milestone		Works Prog		Sea Tunnel So F) - Three Mo	nths A member of the	Date Revision Cheded Approx Shape S

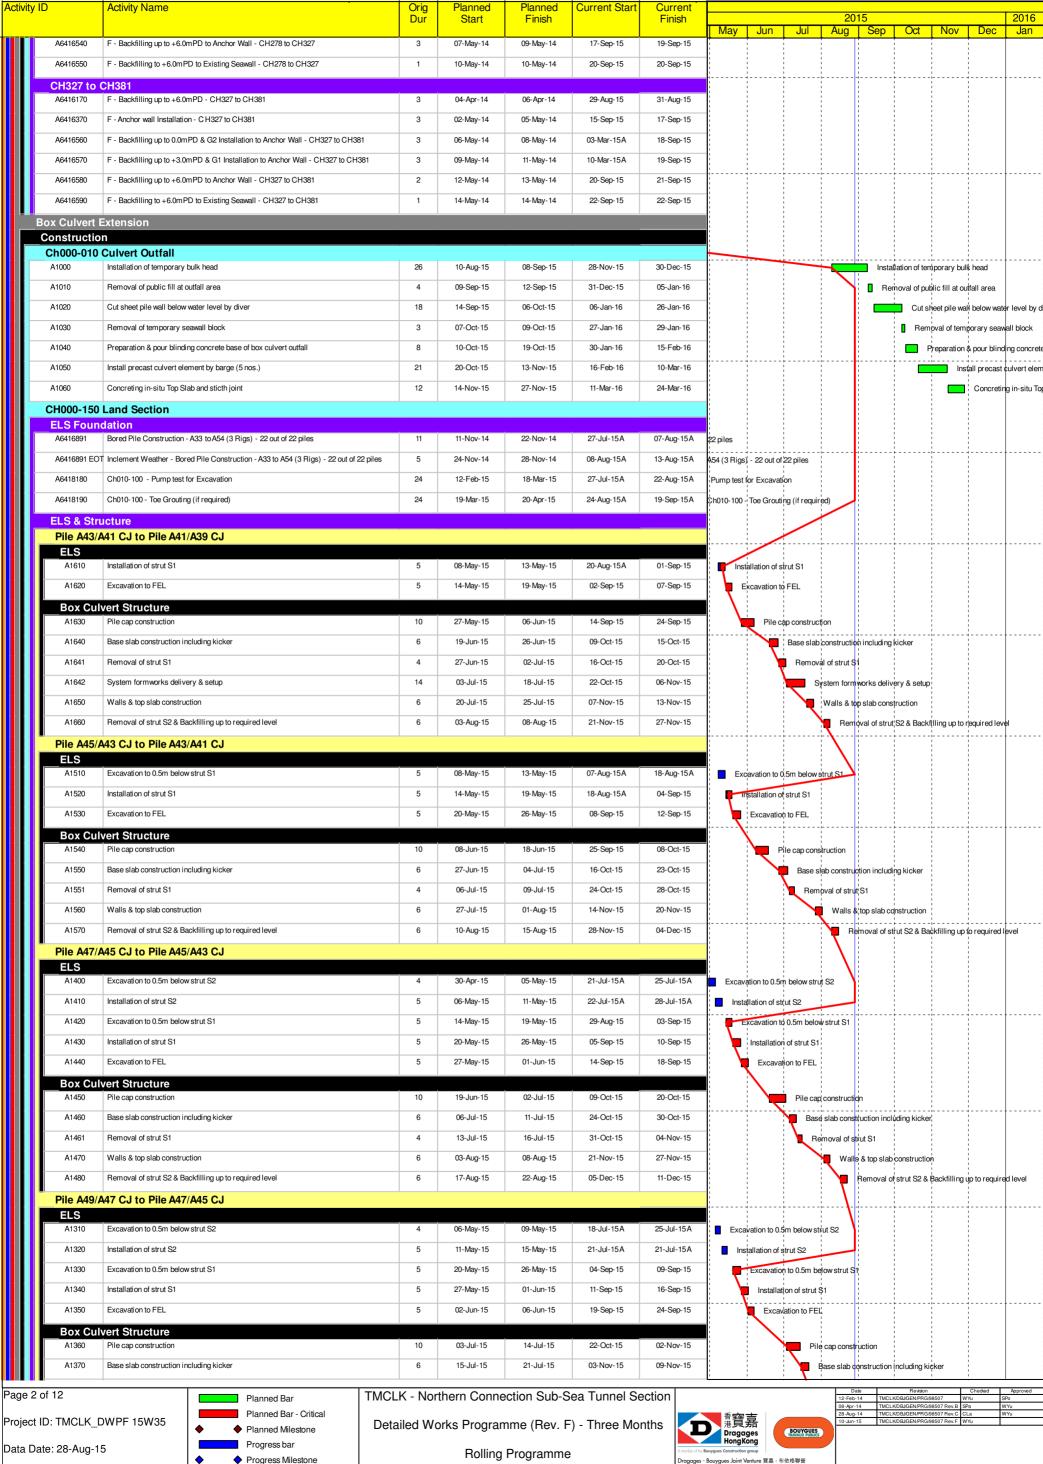


Progress Milestone

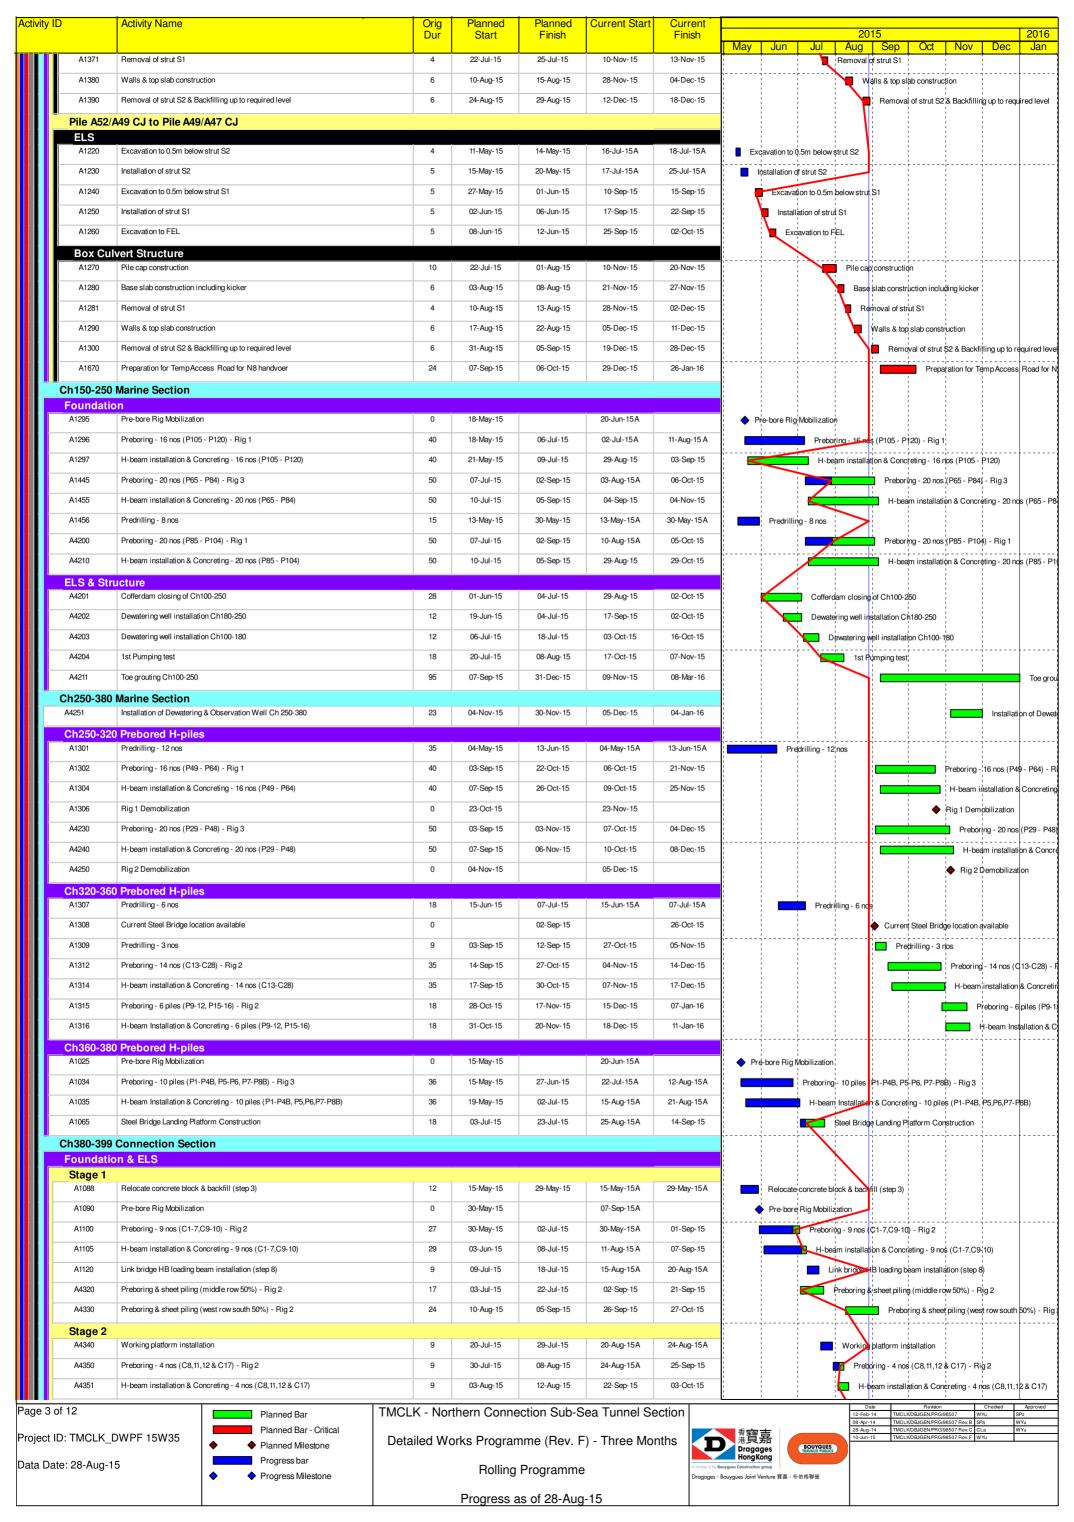

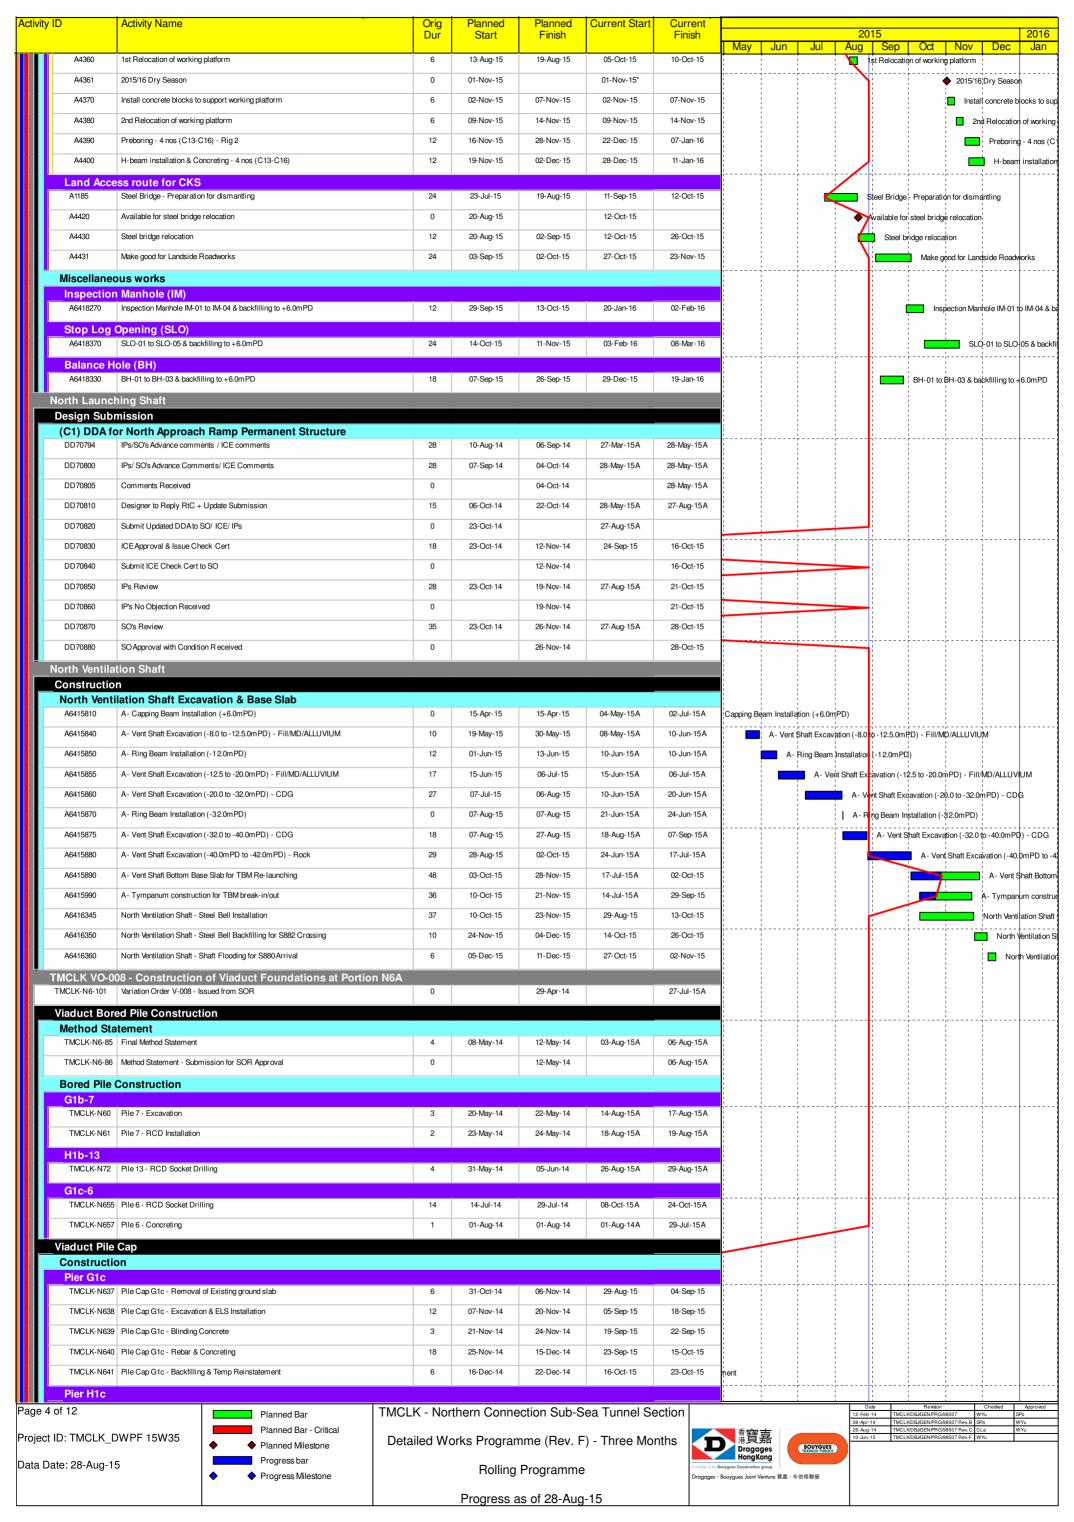

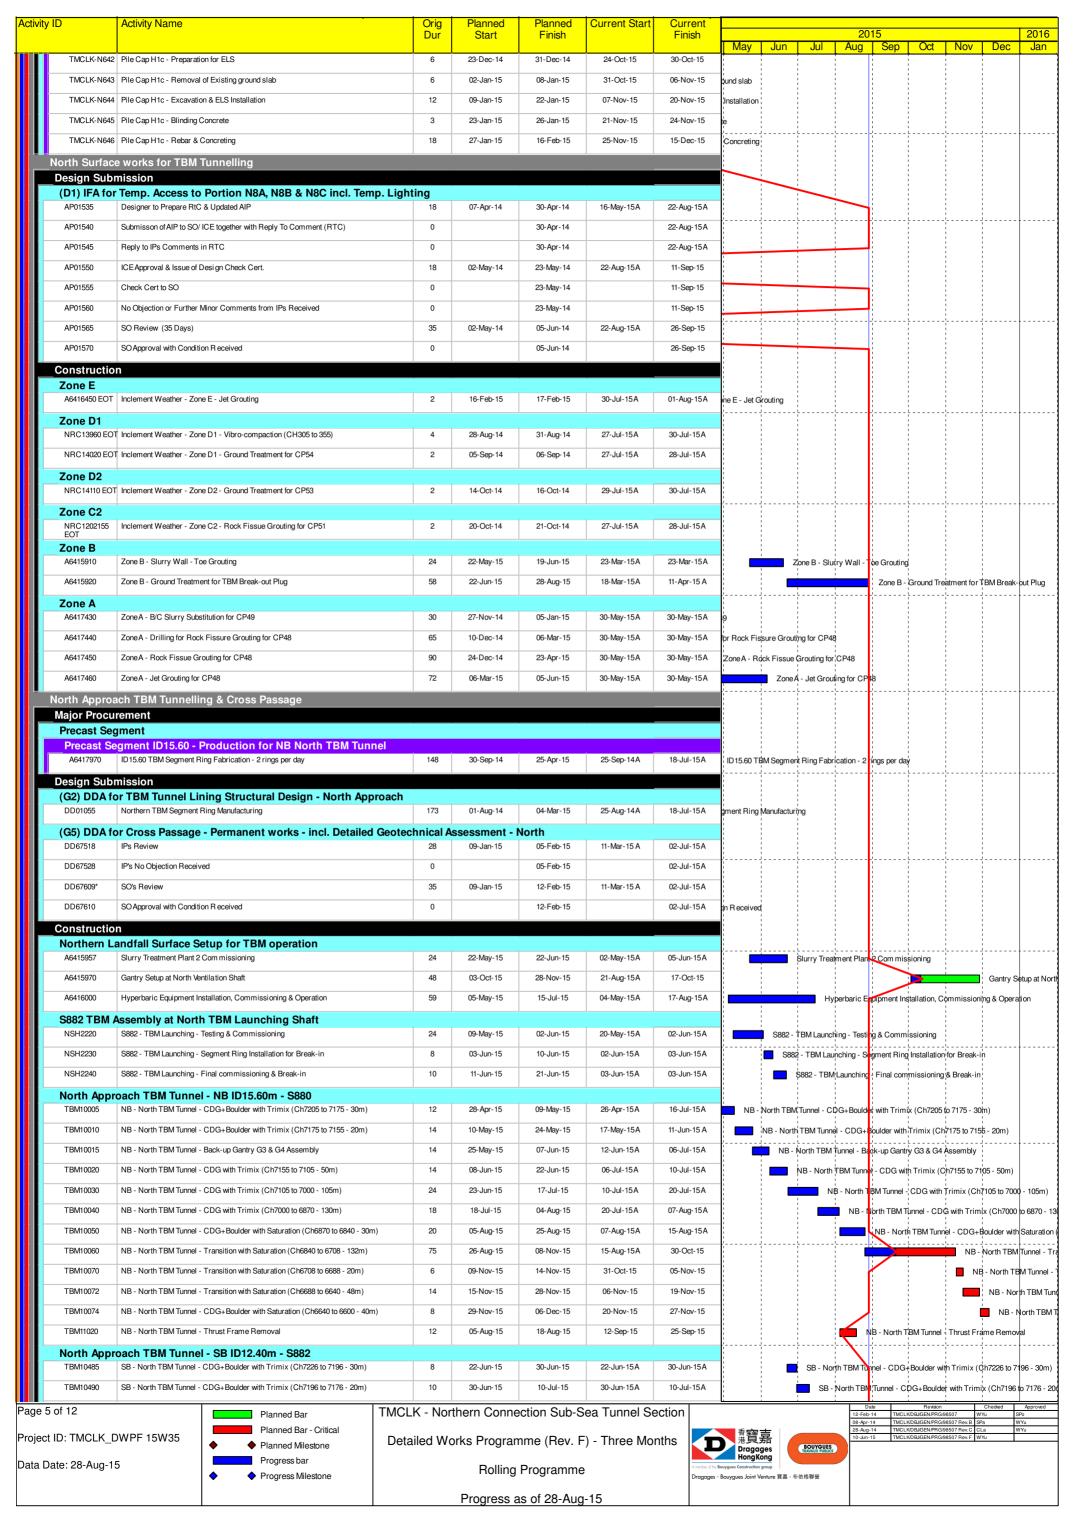

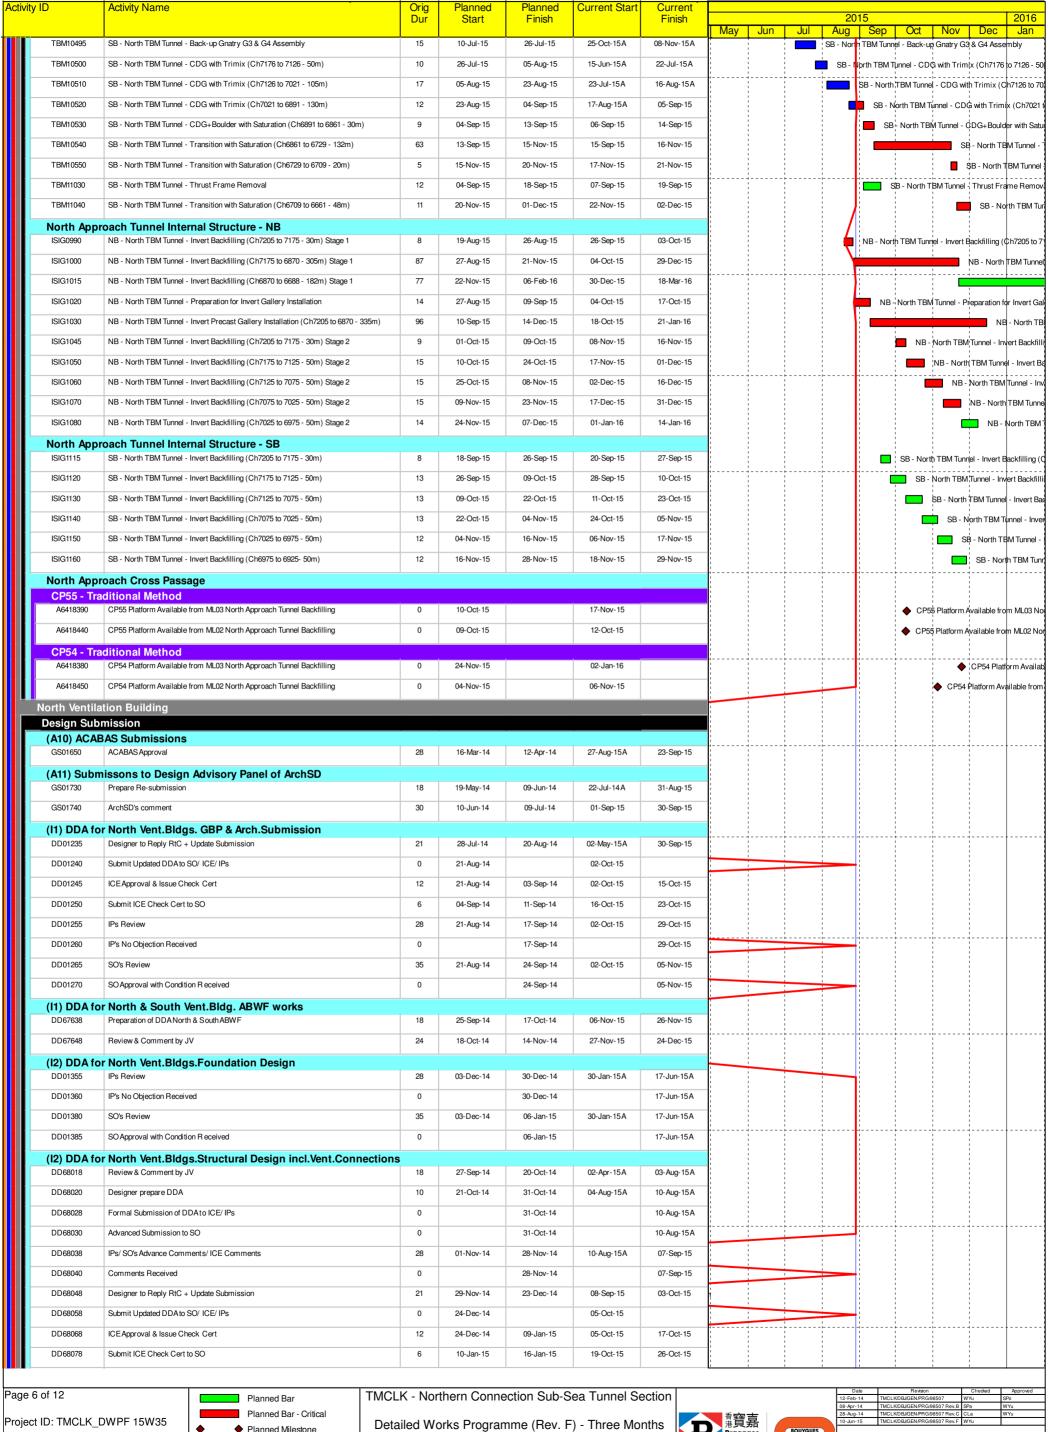

Data Date: 28-Aug-15

Planned Milestone Progress bar Progress Milestone

Rolling Programme





12-Feb-14	TMCLK/DBJGEN/PRG/98507	WYu	SPo .
08-Apr-14	TMCLK/DBJGEN/PRG/98507 Rev. B	SPa	WYu
28-Aug-14	TMCLK/DBJ/GEN/PRG/98507 Rev.C	CLa	WYu
10-Jun-15	TMCLK/DBJGEN/PRG/98507 Rev. F	WYu	


ty ID	Activity Name	Orig	Planned	Planned	Current Start	Current		2015
		Dur	Start	Finish		Finish	May	2015 2 Jun Jul Aug Sep Oct Nov Dec
DD68088	IPs Review	28	24-Dec-14	20-Jan-15	05-Oct-15	01-Nov-15		
DD68098	IP's No Objection Received	0		20-Jan-15		01-Nov-15		
DD68210	SO's Review	35	24-Dec-14	27-Jan-15	05-Oct-15	08-Nov-15		
DD68220	SO Approval with Condition R eceived	0		27-Jan-15		09-Nov-15	peived	
(I3) DDA fo	or North & South Vent.Bldgs. Service and E&M Provision							
DD01600	Preparation of DDANth VB Service and E&MS Provision	18	12-Sep-14	04-Oct-14	01-Jul-15A	31-Aug-15		
DD01605	Review & Comment by JV	24	06-Oct-14	01-Nov-14	01-Sep-15	29-Sep-15		
DD01610	Designer prepare DDA	15	03-Nov-14	19-Nov-14	30-Sep-15	17-Oct-15		
DD01615	Formal Submission of DDAto ICE/ IPs	0		19-Nov-14	·	17-Oct-15		<u> </u>
DD01620	Advanced Submission to SO	0		19-Nov-14		17-Oct-15		
			20.11		10.0			
DD01625	IPs/ SO's Advance Comments/ ICE Comments	28	20-Nov-14	17-Dec-14	18-Oct-15	14-Nov-15	7	
DD01630	Comments Received	0		17-Dec-14		14-Nov-15		
DD01635	Designer to Reply RtC + Update Submission	21	18-Dec-14	14-Jan-15	16-Nov-15	09-Dec-15	omission	
(J1) DDA T	emp.works for Construction of Nth.Vent.Bldg.							
DD04390	Review & Comment by JV	18	13-Oct-14	01-Nov-14	08-May-15A	31-Aug-15		
DD04400	Designer prepare DDA	10	03-Nov-14	13-Nov-14	01-Sep-15	11-Sep-15		
DD04410	Formal Submission of DDAto ICE/ IPs	0		13-Nov-14		11-Sep-15		
DD04420	Advanced Submission to SO	0		13-Nov-14		11-Sep-15		
DD04430	IPs/ SO's Advance Comments/ ICE Comments	28	14-Nov-14	11-Dec-14	12-Sep-15	09-Oct-15		
DD04440	Comments Received	0		11-Dec-14		09-Oct-15		
			40 D		10.0:15			
DD04450	Designer to Reply RtC + Update Submission	21	12-Dec-14	08-Jan-15	10-Oct-15	04-Nov-15	vission	
DD04460	Submit Updated DDA to SO/ ICE/ IPs	0	09-Jan-15		05-Nov-15			
DD04470	ICEApproval & Issue Check Cert	12	09-Jan-15	22-Jan-15	05-Nov-15	18-Nov-15		
DD04480	Submit ICE Check Cert to SO	6	23-Jan-15	29-Jan-15	19-Nov-15	25-Nov-15		
DD04490	IPs Review	28	09-Jan-15	05-Feb-15	05-Nov-15	02-Dec-15		
DD04540	SO's Review	35	09-Jan-15	12-Feb-15	05-Nov-15	09-Dec-15		
(J2) Tower	Crane Foundation for Ventilation Building Preparation of DDATower Crane Foundation for Vent Bldg Construction	18	01-Jun-15	22-Jun-15	01-Jul-15A	06-Jul-15A		Preparation of DDATewer Crane Foundation for Vent Bldg Construction
DD70490	Review & Comment by JV	18	23-Jun-15	14-Jul-15	06-Jul-15A	09-Jul-15A	ļ	-
	,							Review & Comment by JV
DD70500	Designer prepare DDA	10	15-Jul-15	25-Jul-15	09-Jul-15A	09-Jul-15A		Designer prepare DDA
DD70510	Formal Submission of DDAto ICE/ IPs	0		25-Jul-15		09-Jul-15A		♦ Formal Submission of DDAto ICE/ IPs
DD70520	Advanced Submission to SO	0		25-Jul-15		09-Jul-15A		♦ Advanced Submission to SO
DD70530	IPs/ SO's Advance Comments/ ICE Comments	28	26-Jul-15	22-Aug-15	09-Jul-15A	22-Jul-15A		(Ps/SO's Advance Comments/ ICE Comments
DD70540	Comments Received	0		22-Aug-15		22-Jul-15A		♦ Comments Received
DD70550	Designer to Reply RtC + Update Submission	21	24-Aug-15	16-Sep-15	22-Jul-15A	22-Jul-15A		Designer to Reply RtC + Update Submit
DD70560	Submit Updated DDA to SO/ ICE/ IPs	0	17-Sep-15		22-Jul-15A			
	·							Submit Updated DDAto \$0/ ICE/ IPs
DD70570	ICEApproval & Issue Check Cert	12	17-Sep-15	02-Oct-15	22-Jul-15A	22-Jul-15A		ICE Approval & Issue Check Cert
DD70580	Submit ICE Check Cert to SO	6	03-Oct-15	09-Oct-15	22-Jul-15A	22-Jul-15A		Submit ICE Check Cert to SO
DD70590	IPs Review	28	17-Sep-15	14-Oct-15	22-Jul-15A	22-Jul-15A		IPs Review
DD70600	IP's No Objection Received	0		14-Oct-15		22-Jul-15A		◆ IP's No Objection Received
DD70640	SO's Review	35	17-Sep-15	21-Oct-15	22-Jul-15A	22-Jul-15A		\$O's Review
DD70650	SO Approval with Condition R eceived	0		22-Oct-15		22-Jul-15A		SO Approval with Condition
(C2) DDA f	or North Vent Shaft & Duct Permanent Structure							
DD67278	Review & Comment by JV	18	28-Aug-14	18-Sep-14	08-Apr-15A	31-Aug-15		
DD67280	Designer prepare DDA	10	19-Sep-14	30-Sep-14	01-Sep-15	11-Sep-15		
			Сор-14	·	J. 30p-10	·		
DD67288	Formal Submission of DDAto ICE/ IPs	0		30-Sep-14		11-Sep-15		
DD67290	Advanced Submission to SO	0		30-Sep-14		11-Sep-15		
DD67298	IPs/ SO's Advance Comments/ ICE Comments	28	01-Oct-14	28-Oct-14	12-Sep-15	09-Oct-15		
DD67300	Comments Received	0		28-Oct-14		09-Oct-15		
DD67308	Designer to Reply RtC + Update Submission	21	29-Oct-14	21-Nov-14	10-Oct-15	04-Nov-15		
DD67318	Submit Updated DDA to SO/ ICE/ IPs	0	22-Nov-14		05-Nov-15			
DD67328	· ·	12	22-Nov-14	05-Dec-14	05-Nov-15	18-Nov-15		
	ICEApproval & Issue Check Cert							
DD67338	Submit ICE Check Cert to SO	6	06-Dec-14	12-Dec-14	19-Nov-15	25-Nov-15		.
DD67348	IPs Review	28	22-Nov-14	19-Dec-14	05-Nov-15	02-Dec-15		
DD67368	SO's Review	35	22-Nov-14	26-Dec-14	05-Nov-15	09-Dec-15		
North Surfac	ce Roadworks, Utility & Drainage works							
Design Sub								
	for Traffic Sign, Road Marking, Street Furnitures, Sign Ga			44 1	40.4	04 4 45	ļ	
DD01755	SO's Review	35	11-Dec-14	14-Jan-15	10-Apr-15A	31-Aug-15		
DD01760	SO Approval with Condition R eceived	0		14-Jan-15		31-Aug-15	q	
	or Sewerage, Drainage, Waterworks & Utility works for No				-			
DD02135	Designer to Reply RtC + Update Submission	21	15-Oct-14	07-Nov-14	09-Feb-15A	31-Aug-15		
DD02140	Submit Updated DDA to SO/ ICE/ IPs	0	08-Nov-14		01-Sep-15			
DD02145	ICEApproval & Issue Check Cert	12	08-Nov-14	21-Nov-14	01-Sep-15	14-Sep-15		
DD02150	Submit ICE Check Cert to SO	6	22-Nov-14	28-Nov-14	15-Sep-15	21-Sep-15		
DD02155	IPs Review	28	08-Nov-14	05-Dec-14	01-Sep-15	28-Sep-15		
			00 140V-14		0. Sup-10			
DD02160	IP's No Objection Received	0		05-Dec-14		28-Sep-15		
DD02165	SO's Review	35	08-Nov-14	12-Dec-14	01-Sep-15	05-Oct-15		
7 of 12	Planned Bar TMC	CLK - Nor	thern Conne	ection Sub-S	Sea Tunnel Se	ection		Date Revision Cheded Ap 12-Feb-14 TMCLK/DBUGEN/PRG/98507 WYU SPO 08-8p.14 TMCLK/DBUGEN/PRG/98507 Rev R SPa WYU
4 ID: T\$400 11	Planned Bar - Critical						香宝	08-Apr-14 TMCLK/DBJGEN/PRG/98507 Rev. B SPa WYu 28-Aug-14 TMCLK/DBJGEN/PRG/98507 Rev. C CLa WYu
t ID: TMCLK_I	DWPF 15W35 ♦ Planned Milestone De	tailed W	orks Prograr	nme (Rev. F	r) - Three Moi	nths	香寶 港寶 Dragag Hong K	30-Jun-15 TMCLK/DBJGEN/PRG/98507 Rev.F WYu
	Progress bar						HongK	Kong


Data Date: 28-Aug-15


Progress bar ♦ Progress Milestone

Rolling Programme Progress as of 28-Aug-15



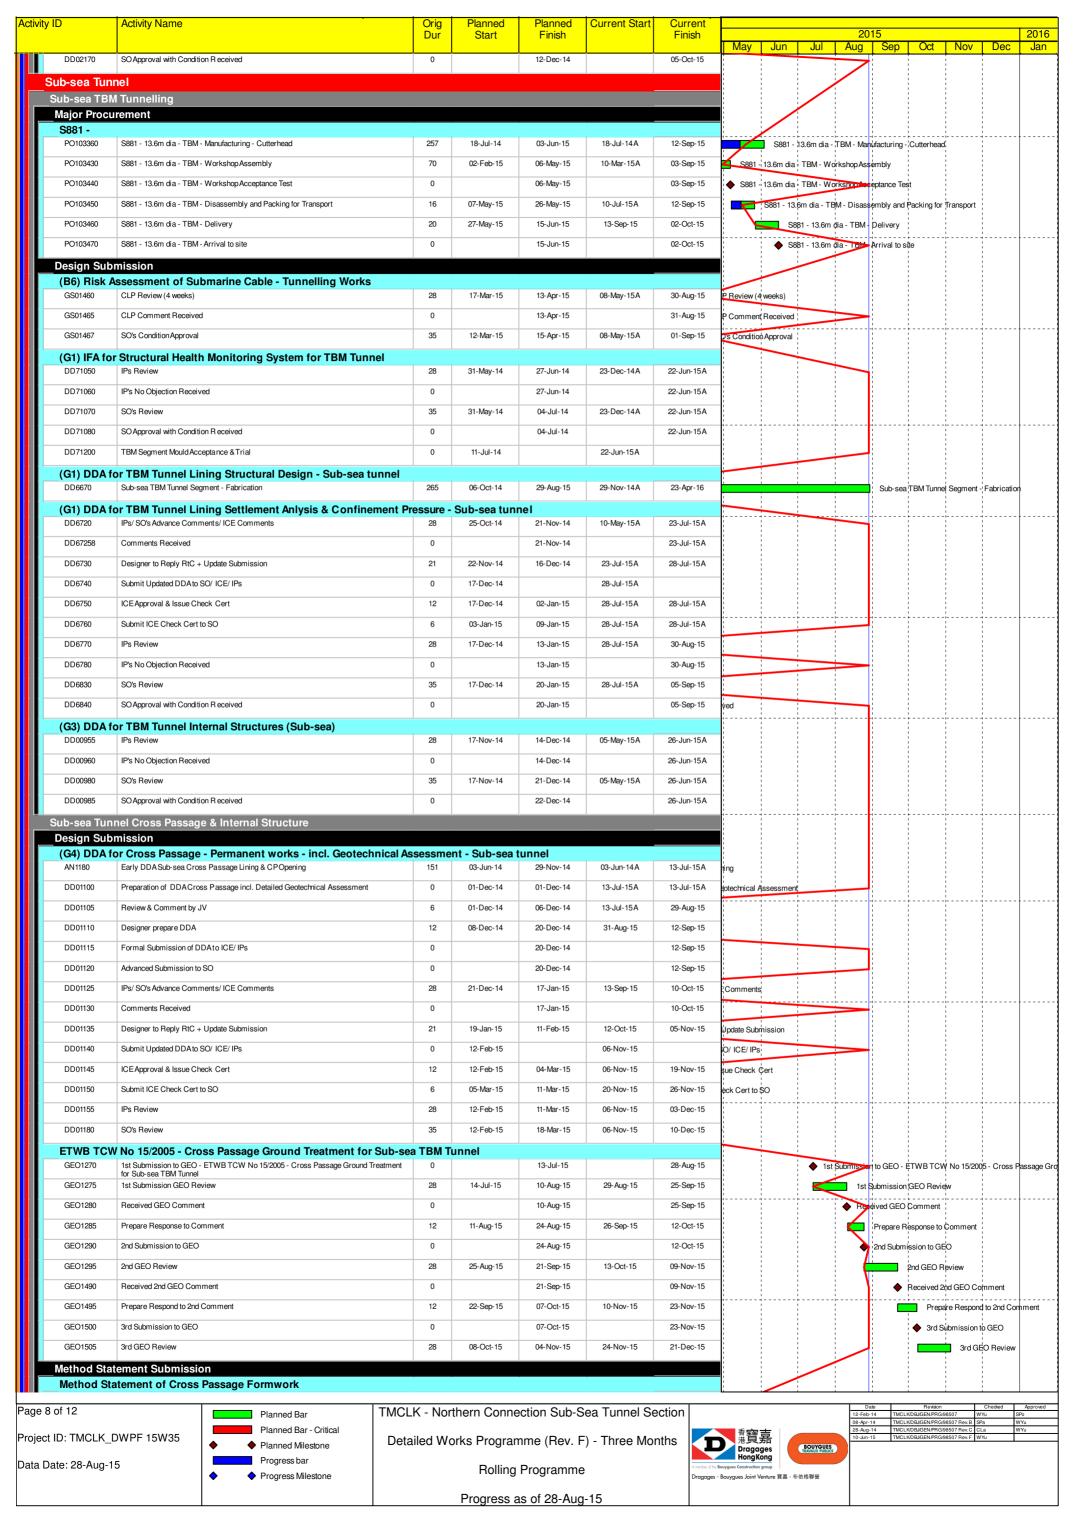

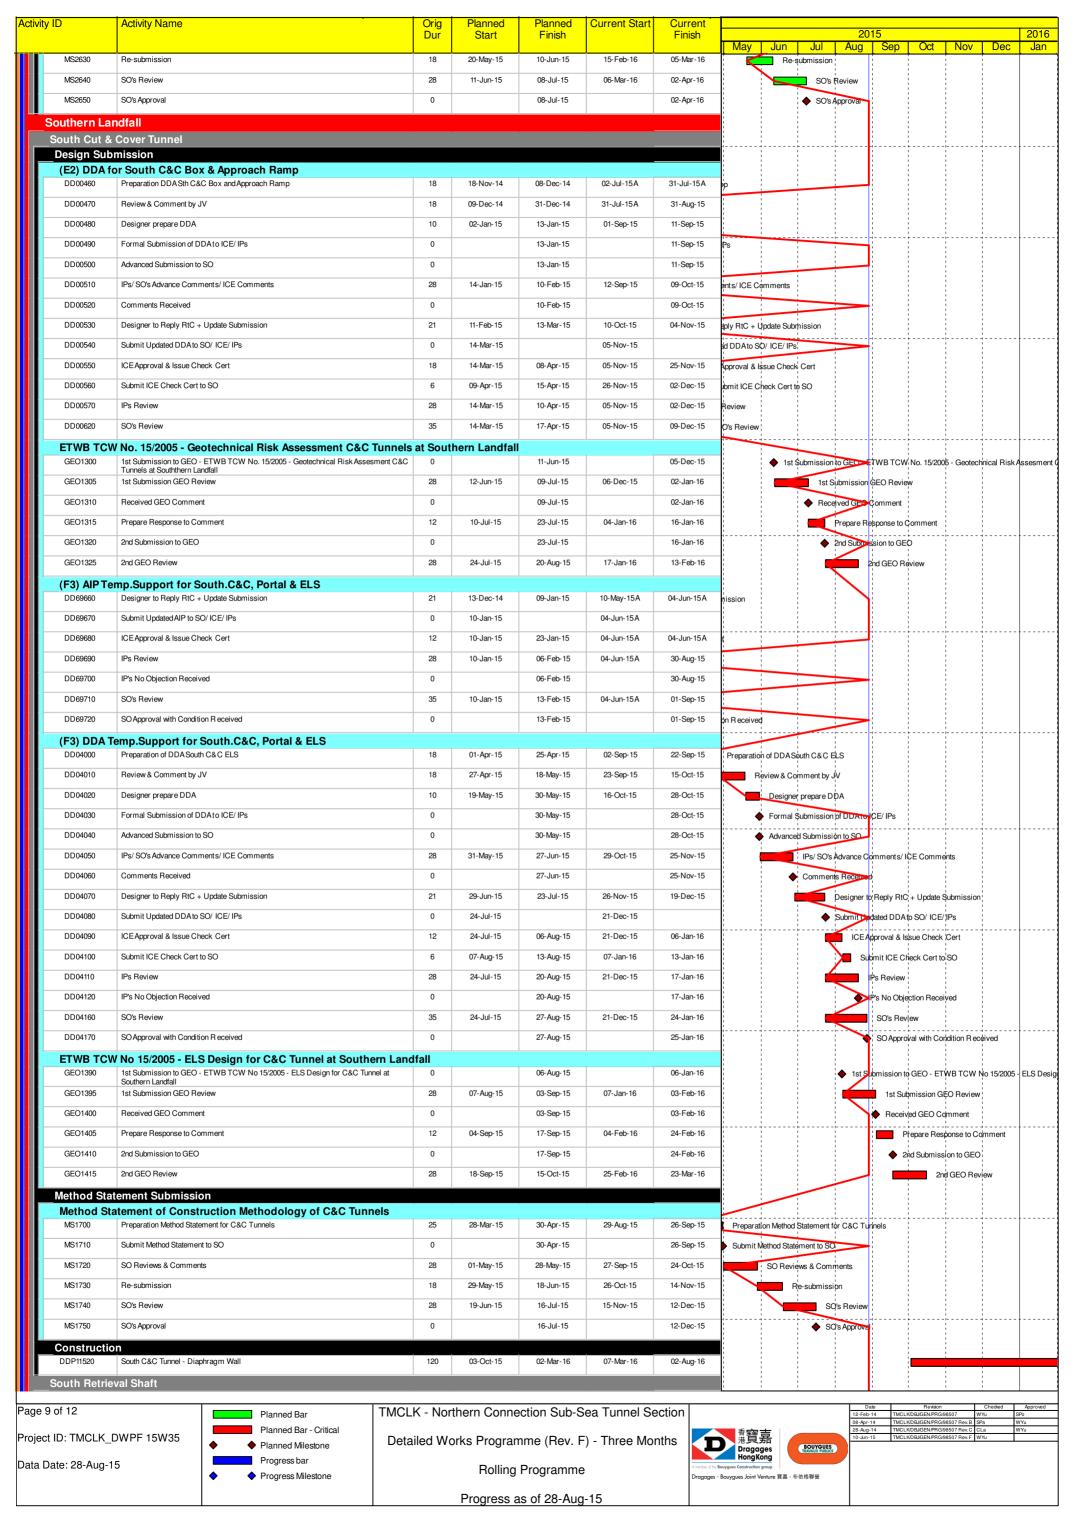

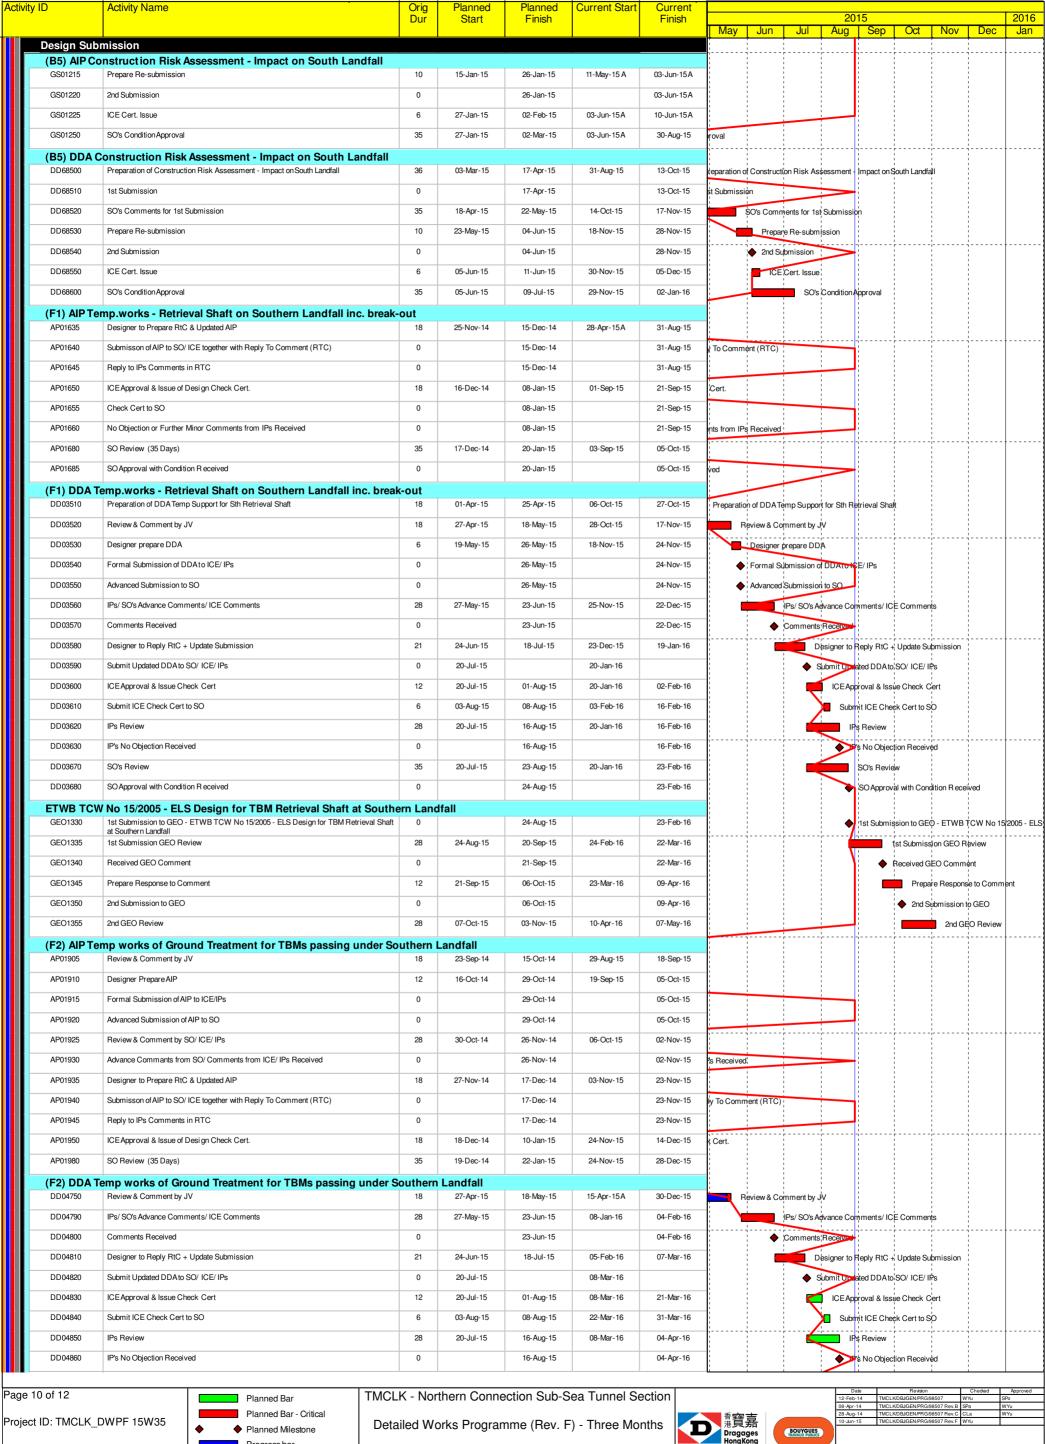


Progress bar Data Date: 28-Aug-15 Progress Milestone

Rolling Programme



12-Feb-14	TMCLK/DBJGEN/PRG/98507	WYu	SPo
08-Apr-14	TMCLK/DBJGEN/PRG/98507 Rev. B	SPa	WYu
28-Aug-14	TMCLK/DBJ/GEN/PRG/98507 Rev.C	CLa	WYu
10-Jun-15	TMCLK/DBJGEN/PRG/98507 Rev. F	WYu	
		-	

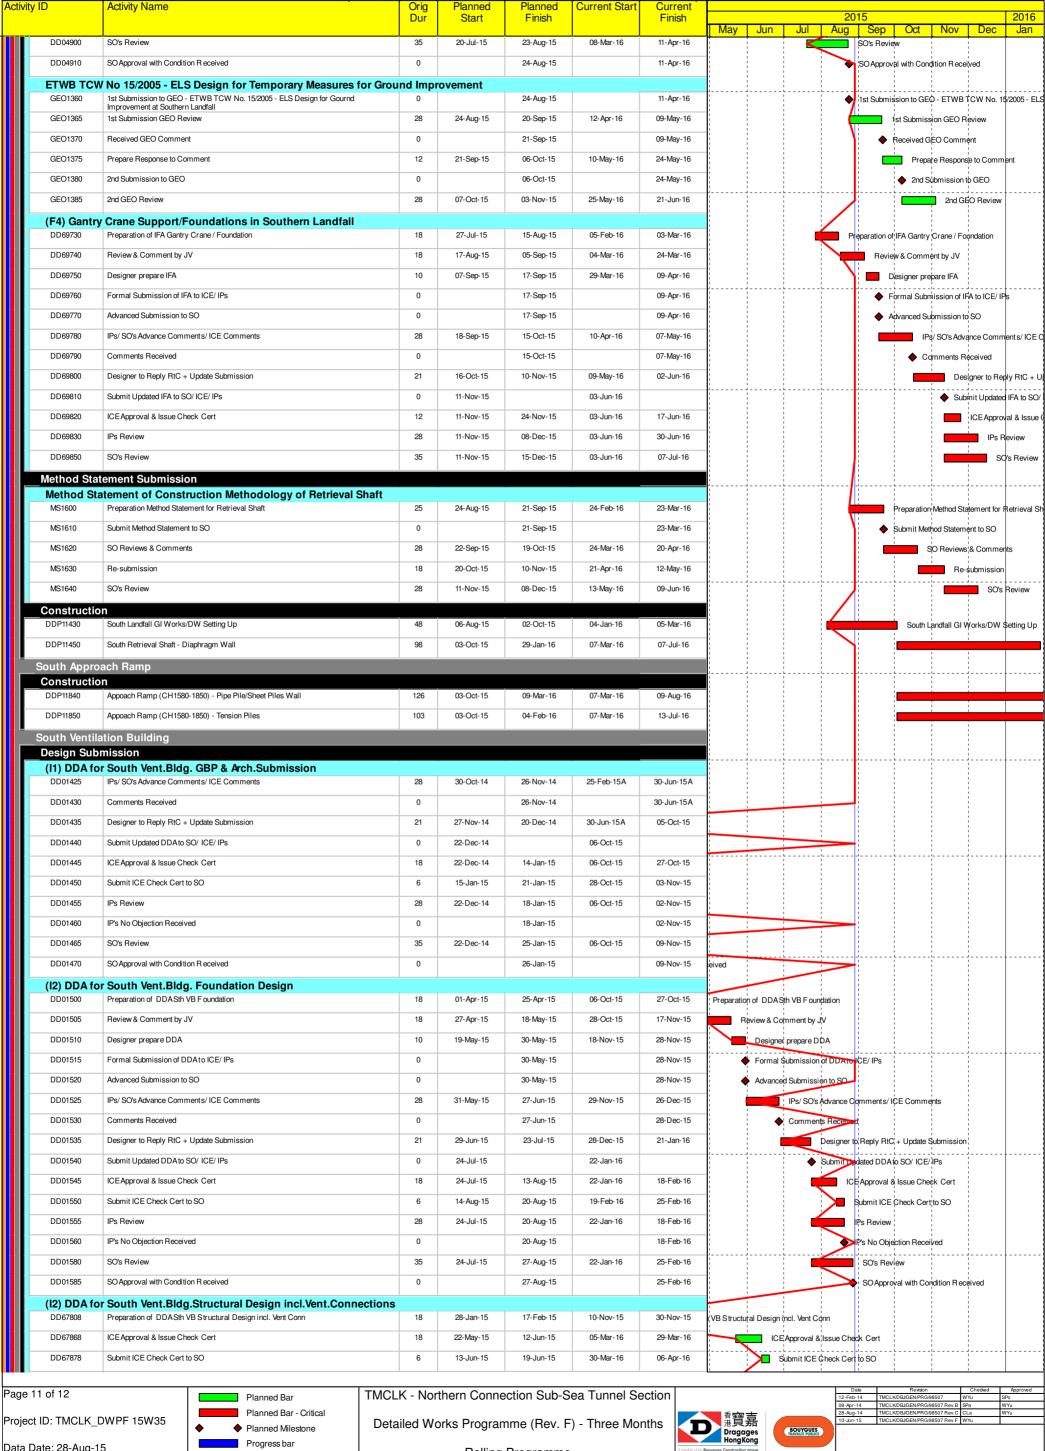


Data Date: 28-Aug-15 Progress Milestone

Rolling Programme





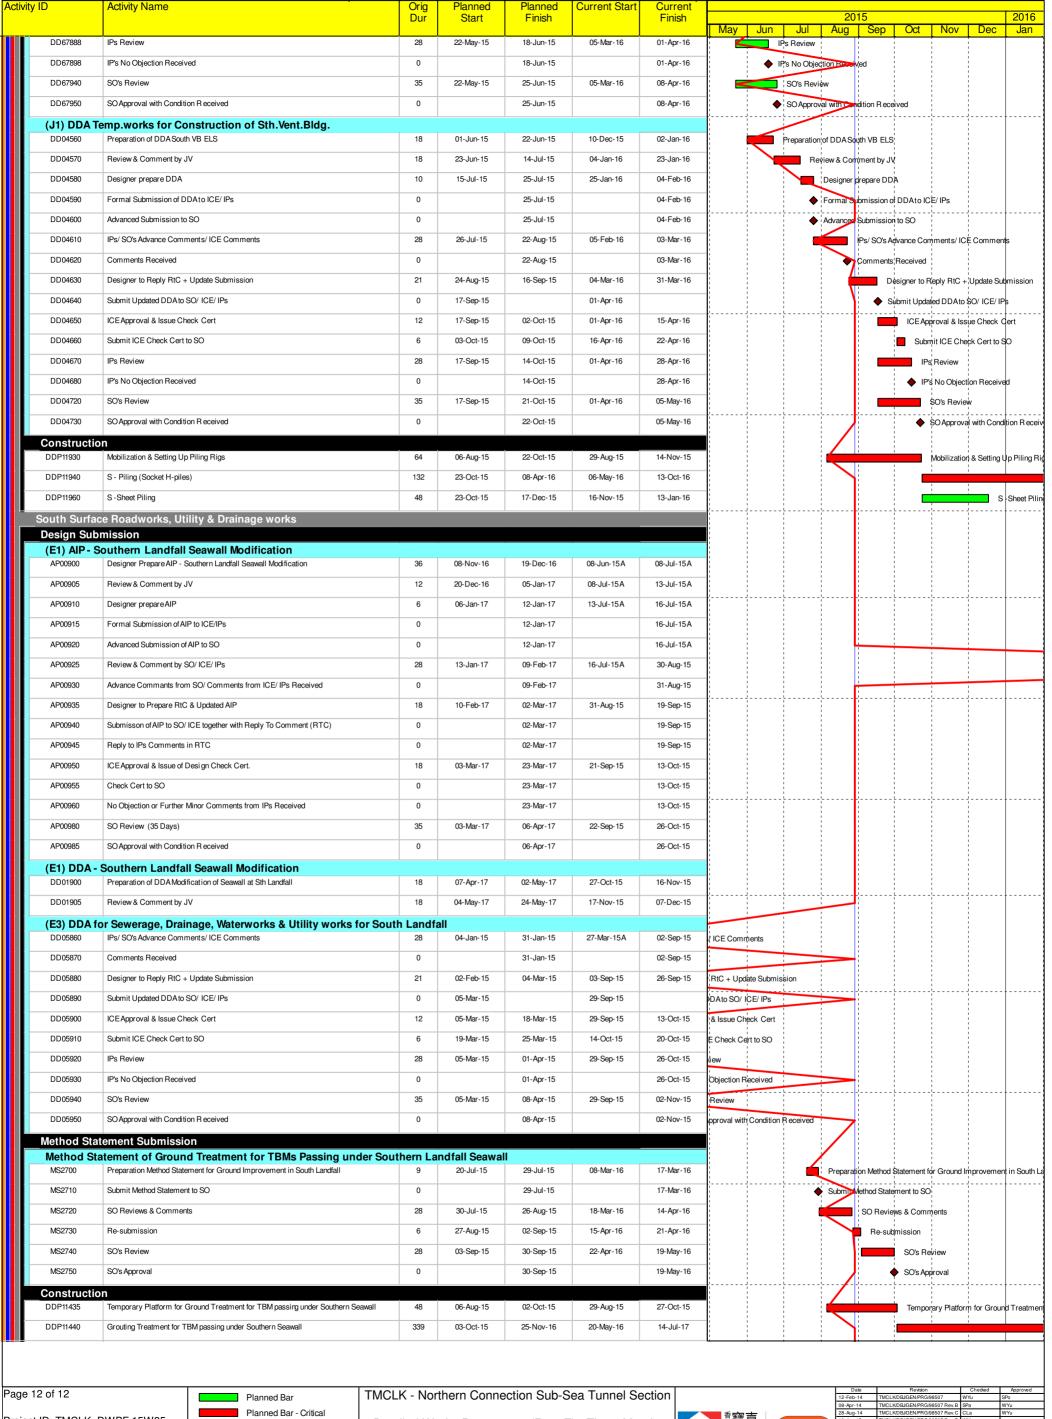

Project ID: TMCLK_DWPF 15W35 Planned Milestone Progress bar Data Date: 28-Aug-15 Progress Milestone

Detailed Works Programme (Rev. F) - Three Months Rolling Programme

Progress as of 28-Aug-15



BOUYGUES TRAVAUX PUBLICS

Date	Revision	Checked	Approved
12-Feb-14	TMCLK/DBJ/GEN/PRG/98507	WYu	SPo
08-Apr-14	TMCLK/DBJ/GEN/PRG/98507 Rev.B	SPa	WYu
28-Aug-14	TMCLK/DBJGEN/PRG/98507 Rev. C	CLa	WYu
10-Jun-15	TMCLK/DBJGEN/PRG/98507 Rev. F	WYu	

Appendix C

Environmental Mitigation and Enhancement Measure Implementation Schedules

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp	lementat Stages	tion	Status *
	Reference					D	С	0	
Air Quality									
4.8.1	3.8	An effective watering programme of twice daily watering with complete coverage, is estimated to reduce by 50%. This is recommended for all areas in order to reduce dust levels to a minimum;	construction period	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		*
4.8.1	3.8	Watering of the construction sites in Lantau for 8 times/day and in Tuen Mun for 12 times/day to reduce dust emissions by 87.5% and 91.7% respectively and shall be undertaken.		Contractor	TMEIA Avoid dust generation		Y		√
4.8.1	3.8	The Contractor shall, to the satisfaction of the Engineer, install effective dust suppression measures and take such other measures as may be necessary to ensure that at the Site boundary and any nearby sensitive receiver, dust levels are kept to acceptable levels.		Contractor	TMEIA Avoid dust generation		Y		*
4.8.1	3.8	The Contractor shall not burn debris or other materials on the works areas.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8. 1	3.8	In hot, dry or windy weather, the watering programme shall maintain all exposed road surfaces and dust sources wet.	All unpaved haul roads / throughout construction period in hot, dry or windy weather	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		✓
4.8.1	3.8	Where breaking of oversize rock/concrete is required, watering shall be implemented to control dust. Water spray shall be used during the handling of fill material at the site and at active cuts, excavation and fill sites where dust is likely to be created.	. 0	Contractor	TMEIA Avoid dust generation		Y		<>
4.8. 1	3.8	Open dropping heights for excavated materials shall be controlled to a maximum height of 2m to minimise the fugitive dust arising from unloading.		Contractor	TMEIA Avoid dust generation		Y		√
4.8.1	3.8	During transportation by truck, materials shall not be loaded to a level higher than the side and tail boards, and shall be dampened or covered before transport.	. 0	Contractor	TMEIA Avoid dust generation		Y		*

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imj	plementa Stages	tion	Status *
	Reference					D	С	O	
4.8.1	3.8	Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards.	construction period	Contractor	TMEIA Avoid dust generation		Y		~
4.8.1	3.8	No earth, mud, debris, dust and the like shall be deposited on public roads. Wheel washing facility shall be usable prior to any earthworks excavation activity on the site.		Contractor	TMEIA Avoid dust		Y		√
4.8.1	3.8	Areas of exposed soil shall be minimised to areas in which works have been completed shall be restored as soon as is		Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	All stockpiles of aggregate or spoil shall be enclosed or covered and water applied in dry or windy condition.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.11	Section 3	EM&A in the form of 1 hour and 24 hour dust monitoring and site audit.	All representative existing ASRs / throughout construction period	Contractor	EM&A Manual		Y		√
WATER QUAL									
Marine Works (Seq	uence A)								
6.1	Annex A	Construction of seawalls to be advanced by at least 200m before the main reclamation dredging and filling can commence. The protection by advanced seawall is a dynamic process depending on the progress of the construction activities and the stage when such protection could be realised is illustrated in Figure 6.2a and detailed in Appendix D6a. The part of the works where such measures can be undertaken for the majority of the time includes the following locations:	backfilling works	Contractor	TM-EIAO		Y		~
Figure 6.2a Appendix D6a		- TM-CLKL northern reclamation;							
6.1	-	a maximum of 50% public fill to be used for all seawall filling below +2.5mPD for TM-CLKL southern and northern landfalls.	TM-CLKL seawall filling	Contractor	TM-EIAO		Y		√

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp	olementa Stages	tion	Status *
	Reference					D	C	O	
6.1	-	a maximum of 30% public fill to be used for reclamation filling below +2.5mPD for TM-CLKL southern landfall	TM-CLKL southern landfall reclamation filling	Contractor	TM-EIAO		Y		N/A
6.1	-	a maximum of 100% public fill to be used for reclamation filling below +2.5mPD for TM-CLKL northern landfall	TM-CLKL northern landfall reclamation filling	Contractor	TM-EIAO		Y		√
6.1	-	Use of cage type silt curtains round allgrab dredgers during the HKBCF, HKLR and TM-CLKL southern reclamation works.	All areas dredging works	Contractor	TM-EIAO		Y		✓
	Figure 1.1 of Annex C	A layer of floating type silt curtain will be applied when dredging and reclamation works are being undertaken at Portion N-a as shown in Figure 1.1 of Annex C of the EM&A Manual.	. 0	Contractor	TM-EIAO		Y		√
6.1	-	Trailer suction hopper dredgers shall not allow mud to overflow.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		~
6.1	-	The use of Lean Material Overboard (LMOB) systems shall be prohibited.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		√
6.1	Annex A	For other parts of the reclamation works construction of seawalls to be advanced by at least 200m before the main reclamation dredging and filling can commence. It should be noted that the protection by advanced seawall is a dynamic process depending on the progress of the construction activities and the stage when such protection could be realised is illustrated in Figure 6.2b and detailed in Appendices D6b. The part of the works where such measures can be undertaken for the majority of the time includes the following locations:	Portion D of HKBCF and HKLR	Contractor	TM-EIAO		Y		*
Figure 6.2b Appendix D6b		 TM-CLKL northern reclamation; Reclamation filling for Portion D of HKBCF; Reclamation filling for FSD berth of HKBCF; and 							

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp	olementa Stages	tion	Status *
	Reference					D	C	O	
		 Reclamation dredging and filling for Portion 1 of HKLR; 							
6.1	-	The filling material for the other parts of the works are the same as Sequence A;	All other areas/backfilling works	Contractor	TM-EIAO		Y		N/A
6.1	5. <i>7</i>	Cage type silt curtain (with steel enclosure) shall be used for grab dredgers working in the site of HKBCF and TM- CLKL southern reclamation. Cage type silt curtains will be applied round all grab dredgers at other works area.	grab dredging	Contractor	TM-EIAO		Y		✓
6.1	Annex A	A layer of floating type silt curtain will be applied around all works as defined in Appendix D6b.	All areas/ through out marine works	Contractor	TM-EIAO		Y		1
6.1	-	TM-CLKL northern landfall: - Reclamation filling shall not proceed until at least 200m section of leading seawall at both the east and west sides of the reclamation are formed above +2.5 mPD, except for 100m gaps for marine access;		Contractor	TM-EIAO		Y		· ·
General Marine Wo	orks		-	-			-		
6.1	-	Use of TMB for the construction of the submarine tunnel.	Tunnel works / Construction phase	Contractor	TM-EIAO		Y		N/A
6.1	-	Export dredged spoils from NWWCZ.	All areas as much as possible / dredging activities	Contractor	DASO Permit conditions		Y		✓
6.1	-	Where public fill is proposed for filling below +2.5mPD, the fine content in the public fill will be controlled to 25%	All areas/ backfilling works	Contractor	TM-EIAO		Y		N/A
6.1	-	Where sand fill is proposed for filling below +2.5mPD, the fine content in the sand fill will be controlled to 5%.	All areas/ backfilling works	Contractor	TM-EIAO		Y		N.A
6.1	-	Mechanical grabs shall be designed and maintained to avoid spillage and should seal tightly while being lifted.	All areas/ throughout construction period	Contractor	Marine Fill Committee Guidelines. DASO permit conditions.		Y		~
6.1	-	Barges and hopper dredgers shall have tight fitting seals to their bottom openings to prevent leakage of material.	All areas/ throughout construction period	Contractor	Marine Fill Committee		Y		√

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	-	lementat Stages		Status *
	Reference					D	C	O	
					Guidelines. DASO				
					permit				
					conditions.				
6.1	-	Any pipe leakages shall be repaired quickly. Plant should not	o o	Contractor	Marine Fill		Y		✓
		be operated with leaking pipes.	construction period		Committee				
					Guidelines. DASO				
					permit				
					conditions.				
6.1	-	Loading of barges and hoppers shall be controlled to prevent		Contractor	Marine Fill		Y		✓
		splashing of dredged material to the surrounding water. Barges or			Committee				
		hoppers shall not be filled to a level which will cause overflow of materials or pollution of water during loading or transportation.			Guidelines. DASO				
		inaterials of pollution of water during loading of transportation.			permit				
					conditions.				
6.1	-	Excess material shall be cleaned from the decks and exposed fittings	o o	Contractor	Marine Fill		Y		✓
		of barges and hopper dredgers before the vessel is moved.	construction period		Committee				
					Guidelines. DASO				
					permit				
					conditions.				
6.1	-	Adequate freeboard shall be maintained on barges to reduce the		Contractor	Marine Fill		Y		N/A
		likelihood of decks being washed by wave action;	construction period		Committee				
					Guidelines. DASO				
					permit				
					conditions.				27/
6.1	-	All vessels shall be sized such that adequate clearance is maintained between vessels and the sea bed at all states of the tide		Contractor	Marine Fill Committee		Y		N/A
		to ensure that undue turbidity is not generated by turbulence from							
		vessel movement or propeller wash.			Guidelines. DASO permit				
		1 1			^				
(1		cm 1 1 11 (() 1 1 d	A11 / (1 1		conditions.		3/		4
6.1	-	The works shall not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and		Contractor	Marine Fill Committee		Y		<>
		adjacent to the works site.	construction period						
		adjucent to the works site.			Guidelines. DASO				
			l		permit				

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imj	plementa Stages	tion	Status *
	Reference					D	C	O	
					conditions.				
6.1	5.2	Silt curtain shall have proved effectiveness from the producer and shall be fully maintained throughout the works by the contractor.		Contractor	TM-EIAO		Y		~
6.1	-	The daily maximum production rates shall not exceed those assumed in the water quality assessment.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		√
6.1	-	The dredging and filling works shall be scheduled to spread the works evenly over a working day.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
Land Works				•					•
6.1	-	Wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		√
6.1	-	Sewage effluent and discharges from on-site kitchen facilities shall be directed to Government sewer in accordance with the requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided.	construction period	Contractor	TM-EIAO		Y		√
6.1	-	Storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		*
6.1	-	Silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly including specifically at the onset of and after each rainstorm.		Contractor	TM-EIAO		Y		<>
6.1	-	Temporary access roads should be surfaced with crushed stone or gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		√
6.1	-	Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.		Contractor	TM-EIAO		Y		√

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp	olementat Stages	tion	Status *
	Reference					D	C	О	
6.1	-	Measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		<>
6.1	-	Open stockpiles of construction materials (e.g. aggregates and sand) on site should be covered with tarpaulin or similar fabric during rainstorms.		Contractor	TM-EIAO		Y		√
6.1	5.8	Manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers.	construction period	Contractor	TM-EIAO		Y		√
6.1	-	Discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	. 0	Contractor	TM-EIAO		Y		✓
6.1	-	All vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit.	construction period	Contractor	TM-EIAO		Y		✓
6.1	-	Wheel wash overflow shall be directed to silt removal facilities before being discharged to the storm drain.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.1	-	Section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel.		Contractor	TM-EIAO		Y		√
6.1	-	Wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects.		Contractor	TM-EIAO		Y		√
6.1	-	Vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for off site disposal.	construction period	Contractor	TM-EIAO		Y		N/A

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp	lementa Stages	tion	Status *
	Reference					D	C	O	
6.1	1	The Contractor shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately.		Contractor	TM-EIAO		Y		√
6.1	-	, e	All areas/ throughout construction period	Contractor	TM-EIAO Waste Disposal Ordinance		Υ		✓
6.1	-	All fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank.		Contractor	TM-EIAO		Y		√
6.1	-	1 0 10	All areas/ throughout construction period	Contractor	TM-EIAO		Y		√
6.1	-	Roadside gullies to trap silt and grit shall be provided prior to discharging the stormwater into the marine environment. The sumps will be maintained and cleaned at regular intervals.	Roadside/design and operation	Design Consultant/ Contractor	TM-EIAO	Y		Y	√
6.1	Section 5	All construction works shall be subject to routine audit to ensure implementation of all EIA recommendations and good working practice.		Contractor	EM&A Manual		Y		✓
Water Quality Mor	nitoring						'		
6.1	Section 5		as defined in EM&A Manual, Section 5/ Before, through-out	Contractor	EM&A Manual		Y	Y	√
ECOLOGY									

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Im _l	olementa Stages	tion	Status *
	Reference					D	С	O	
8.14	6.3	Specification for and implement pre, during and post construction dolphin abundance monitoring.	All Areas/Detailed Design/ during construction works/post construction	Design Consultant/ Contractor	TMEIA	Y	Y	Y	√
8.14	6.3,6.5	Specification and implementation of 250m dolphin exclusion zone.	All dredging and reclamation areas/Detailed Design/during all reclamation and dredging works	Design Consultant/ Contractor	TMEIA	Y	Y		·
8.15	6.3, 6.5	Specification and deployment of an artificial reef of an area of 3,600m2 in an area where fishing activities are prohibited.	Area of prohibited fishing activities/Detailed Design/towards end of construction period	TM-CLKL/ HKBCF Design Consultant/TM- CLKL/ HKBCF Contractor	TMEIA	Y		Y	N/A. To be implemente d by AFCD.
8.14	6.3, 6.5	Specification and implementation of marine vessel control specifications	All areas/Detailed Design/during construction works	Design Consultant/ Contractor	TMEIA	Y	Y		√
8.14	6.3, 6.5	Design and implementation of acoustic decoupling methods for dredging and reclamation works	All areas/ Detailed Design/during dredging and reclamation works	Design Consultant/ Contractor	TMEIA	Y	Y		*
8.15	6.3, 6.4	Pre-construction phase survey and coral translocation	Detailed Design/Prior to construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
8.15	6.5	Audit coral translocation success	Post translocation	Contractor	TMEIA		Y		✓
7.13	6.5	The loss of habitat shall be supplemented by enhancement planting in accordance with the landscape mitigation schedule.	All areas / As soon as accessible	Contractor	TMEIA		Y		N/A.
7.13	6.5	Spoil heaps shall be covered at all times.	All areas / Throughout construction period	Contractor	TMEIA		Y		√
7.13	6.5	Avoid damage and disturbance to the remaining and surrounding natural habitat	All areas / Throughout construction period	Contractor	TMEIA		Y		√
7.13	6.5	Placement of equipment in designated areas within the existing disturbed land	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Disturbed areas to be reinstated immediately after completion of the works.	All areas / Throughout construction period	Contractor	TMEIA		Y		√

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Imp	olementa Stages	Status *	
	Reference					D	С	О	
7.13	6.5	Construction activities should be restricted to the proposed works boundary.	All areas / Throughout construction period	Contractor	TMEIA		Y		√
LANDSCAPE A	AND VISUAI	L							
10.9	7.6	The colour and shape of the toll control buildings, ventilation building and administration building shall adopt a design which could blend it into the vicinity elements, and the details will be developed in detailed design stage (DM2)	All areas/detailed design	Design Consultant	TMEIA	Y			N/A
10.9	7.6	Aesthetic design of the viaduct, retaining wall and other structures will be developed under ACABAS submission (DM5)	All areas/detailed design	Design Consultant	TMEIA	Y			N/A
10.9	7.6	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works (CM5)	All areas/detailed design/ during construction/post construction	Design Consultant/ Contractor	TMEIA	Y	Y		√
10.9	7.6	Control night-time lighting and glare by hooding all lights (CM6)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		N/A
10.9	7.6	Ensure no run-off into water body adjacent to the Project Area (CM7)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		√
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (CM8)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Aesthetically pleasing design (visually unobtrusive and non-reflective) as regard to the form, material and finishes shall be incorporated to all buildings, engineering structures and associated infrastructure facilities (OM5)	All areas/detailed design/ during construction / during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (OM6)	All areas/detailed design/ during construction / during operation	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
WASTE									
12.6		The Contractor shall identify a coordinator for the management of waste.	Contract mobilisation	Contractor	TMEIA		Y		√

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual Reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Stages			Status *
10 (Kererence	The Contractor shall groupes and implement a Wester	Contract as shill estima	Combination	TMELA Manle	D	C	0	
12.6		The Contractor shall prepare and implement a Waste Management Plan which specifies procedures such as a ticketing system, to facilitate tracking of loads and to ensure that illegal disposal of wastes does not occur, and protocols for the maintenance of records of the quantities of wastes generated, recycled and disposed. A recording system for the amount of waste generated, recycled and disposed (locations) should be established.		Contractor	TMEIA, Works Branch Technical Circular No. 5/99 for the Trip-ticket System for Disposal of Construction and Demolition Material		Y		·
12.6		The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges.		Contractor	TMEIA, Land (Miscellaneous Provisions) Ordinance (Cap 28); Waste Disposal Ordinance (Cap 354); Dumping at Sea Ordinance (Cap 466); Water Pollution Control Ordinance.		Y		✓
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedures including waste reduction, reuse and recycling.		Contractor	TMEIA		Y		√
12.6	8.1	The extent of cutting operation should be optimised where possible. Earth retaining structures and bored pile walls should be proposed to minimise the extent of cutting.		Contractor	TMEIA		Y		√
12.6	8.1	The surplus surcharge should be transferred to a fill bank	Reclamation areas / after surcharge works	Contractor	TMEIA		Y		N/A
12.6	8.1	Rock armour from the existing seawall should be reused on the new sloping seawall as far as possible	All areas / throughout construction period	Contractor	TMEIA		Y		√
12.6	8.1	The site and surroundings shall be kept tidy and litter free.	All areas / throughout construction period	Contractor	TMEIA		Y		✓

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual		Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
	Reference					D	С	О	
12.6	8.1	No waste shall be burnt on site.	All areas / throughout construction period	Contractor	TMEIA		Y		√
12.6	8.1	Provisions to be made in contract documents to allow and promote the use of recycled aggregates where appropriate.	Detailed Design	Design Consultant	TMEIA	Y			√
12.6	8.1	The Contractor shall be prohibited from disposing of C&D materials at any sensitive locations. The Contractor should propose the final disposal sites in the EMP and WMP for approval before implementation.	construction period	Contractor	TMEIA		Y		~
12.6	8.1	Stockpiled material shall be covered by tarpaulin and /or watered as appropriate to prevent windblown dust/ surface run off.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Excavated material in trucks shall be covered by tarpaulins to reduce the potential for spillage and dust generation.	All areas / throughout construction period	Contractor	TMEIA		Y		√
12.6	8.1	Wheel washing facilities shall be used by all trucks leaving the site to prevent transfer of mud onto public roads.	All areas / throughout construction period	Contractor	TMEIA		Y		√
12.6	8.1	Dredged marine mud shall be disposed of in a gazetted marine disposal ground under the requirements of the Dumping at Seas Ordinance.		Contractor	TMEIA		Y		√
12.6	8.1	Standard formwork or pre-fabrication should be used as far as practicable so as to minimise the C&D materials arising. The use of more durable formwork/plastic facing for construction works should be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should avoid over-ordering and wastage.	construction period	Contractor	TMEIA		Y		V

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	_	olementa Stages		Status *
	Reference					D	С	О	
12.6	8.1	The Contractor should recycle as many C&D materials (this is a waste section) as possible on-site. The public fill and C&D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials. Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.	construction period	Contractor	TMEIA		Y		•
12.6	8.1	All falsework will be steel instead of wood.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Chemical waste producers should register with the EPD. Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows: f suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed; f Having a capacity of <450L unless the specifications have been approved by the EPD; and f Displaying a label in English and Chinese according to the instructions prescribed in Schedule 2 of the Regulations. f Clearly labelled and used solely for the storage of chemical wastes; f Enclosed with at least 3 sides; f Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest; f Adequate ventilation; f Sufficiently covered to prevent rainfall	construction period	Contractor	TMEIA		Y		<>

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	EM&A Manual	Environmental Protection Measures	Agent Location/ Timing Implementation Agent		Relevant Standard or Requirement	Implementation Stages			Status *
	Reference					D	С	O	
		entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and							
		f Incompatible materials are adequately							
		separated.							
12.6	8.1	Waste oils, chemicals or solvents shall not be disposed of to drain,	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Adequate numbers of portable toilets should be provided for on-site workers. Portable toilets should be maintained in reasonable states, which will not deter the workers from utilising them.		Contractor	TMEIA		Y		~
12.6	8.1	Night soil should be regularly collected by licensed collectors.	All areas / throughout construction period	Contractor	TMEIA		Y		N/A
12.6	8.1	General refuse arising on-site should be stored in enclosed bins or compaction units separately from C&D and chemical wastes. Sufficient dustbins shall be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station. Burning of refuse on construction sites is prohibited.	construction period	Contractor	TMEIA		Y		⇔
12.6	8.1	All waste containers shall be in a secure area on hardstanding;	All areas / throughout construction period	Contractor	TMEIA		Y		√
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including waste reduction, reuse and recycling.		Contractor	TMEIA		Y		√
12.6	8.1	Office wastes can be reduced by recycling of paper if such volume is sufficiently large to warrant collection. Participation in a local collection scheme by the Contractor should be advocated. Waste separation facilities for paper, aluminium cans, plastic bottles, etc should be provided on-site.	construction period	Contractor	TMEIA		Y		*

Legend: D=Design, C=Construction, O=Operation

Tuen Mun - Chek Lap Kok Link

Northern Connection Sub-sea Tunnel Section

Environmental Mitigation and Enhancement Measure Implementation Schedule

EIA Reference	Manual	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	-		tion	Status *
	Reference					D	C	O	
12.6	Section 8	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.		Contractor	EM&A Manual		Y		√
CULTURAL HERITAGE									
11.8	Section 9	EM&A in the form of audit of the mitigation measures	All areas / throughout construction period	Highways Department	EIAO-TM	·	Y		N/A

* Remarks:

✓ Compliance of Mitigation Measures

Compliance of Mitigation but need improvement

x Non-compliance of Mitigation Measures

Non-compliance of Mitigation Measures but rectified by Contractor
 Deficiency of Mitigation Measures but rectified by Contractor

N/A Not Applicable in Reporting Period

Legend: D=Design, C=Construction, O=Operation

Appendix D

Summary of Action and Limit Levels

Table D1 Action and Limit Levels for 1-hour and 24-hour TSP

Parameters	Action	Limit
24 Hour TSP Level in μg/m³	ASR1 = 213	260
	ASR5 = 238	
	AQMS1 = 213	
	AQMS2 = 238	
	ASR10 = 214	
1 Hour TSP Level in μg /m³	ASR1 = 331	500
	ASR5 = 340	
	AQMS1 = 335	
	AQMS2 = 338	
	ASR10 = 337	

Table D2 Action and Limit Levels for Water Quality

Parameter	Action Level#	Limit Level#
DO in mg/L (a)	Surface and Middle	Surface and Middle
	5.0 mg/L	4.2 mg/L
	<u>Bottom</u>	<u>Bottom</u>
	4.7 mg/L	3.6 mg/L
Turbidity in NTU (Depthaveraged (b), (c))	120% of upstream control station at the same tide of the same day and 95%-ile of baseline data, i.e.,	130% of upstream control station at the same tide of the same day and 99%-ile of baseline data, i.e.,
	27.5 NTU	47.0 NTU
SS in mg/L (Depth-averaged (b), (c))	120% of upstream control station at the same tide of the same day and 95%-ile of baseline data, i.e., 23.5 mg/L	130% of upstream control station at the same tide of the same day and 10mg/L for WSD Seawater Intakes at Tuen Mun and 99%-ile of baseline data, i.e.,
		34.4 mg/L

Notes:

Baseline data: data from HKZMB Baseline Water Quality Monitoring between 6 and 31 October 2011.

- (a) For DO, non-compliance of the water quality limits occurs when monitoring result is lower than the limits.
- (b) "Depth-averaged" is calculated by taking the arithmetic means of reading of all three depths $\frac{1}{2}$
- (c) For turbidity and SS, non-compliance of the water quality limits occurs when monitoring result is higher than the limits.
- (d) All figures given in the table are used for reference only, and EPD may amend the figures whenever it is considered as necessary
- (e) The 1%-ile of baseline data for surface and middle DO is 4.2 mg/L, whilst for bottom DO is 3.6 mg/L.

Table D3 Action and Limit Levels for Impact Dolphin Monitoring

	North Lantau Social Cluster					
	NEL	NWL				
Action Level	STG < 70% of baseline &	STG < 70% of baseline &				
	ANI < 70% of baseline	ANI < 70% of baseline				
Limit Level	[STG < 40% of baseling	[STG < 40% of baseline & ANI < 40% of baseline]				
		and				
	STG < 40% of baseline & ANI < 40% of baseline					

Notes:

- 1. STG means quarterly encounter rate of number of dolphin sightings, which is **6.00 in NEL** and **9.85 in NWL** during the baseline monitoring period
- 2. ANI means quarterly encounter rate of total number of dolphins, which is **22.19 in NEL** and **44.66 in NWL** during the baseline monitoring period
- 3. For North Lantau Social Cluster, AL will be trigger if NEL or NWL fall below the criteria; LL will be triggered if both NEL and NWL fall below the criteria.

Table D4 Derived Value of Action Level (AL) and Limit Level (LL)

	North Lanta	North Lantau Social Cluster				
	NEL	NWL				
Action Level	STG < 4.2 & ANI< 15.5	STG < 6.9 & ANI < 31.3				
Limit Level	[STG < 2.4 & ANI <8.9]					
	and					
	[STG < 3.9 & ANI <17.9]					

Appendix E

EM&A Monitoring Schedules

HY/2012/08 - Tuen Mun - Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section Air Quality Impact Monitoring Schedule - June 2015

Air quality monitoring stations: ASR1, ASR5, ASR6, ASR10, AQMS1

All quality monitoring static	ons: ASR1, ASR5, ASR6, A 	SKTU, AQWST				
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1-Jun		3-Jun			6-Jun
		1-hour TSP - 3 times			1-hour TSP - 3 times	
		24-hour TSP - 1 time			24-hour TSP - 1 time	
		Impact AQM			Impact AQM	
7-Jun		9-Jun	10-Jun		12-Jun	13-Jun
	1-hour TSP - 3 times			1-hour TSP - 3 times		
	24-hour TSP - 1 time			24-hour TSP - 1 time		
	Impact AQM			Impact AQM		
14-Jun		16-Jun	17-Jun		19-Jun	Public Holiday 20-Jun
1-hour TSP - 3 times	10 00		1-hour TSP - 3 times	10 00.11	10 00.1	1-hour TSP - 3 times
24-hour TSP - 1 time			24-hour TSP - 1 time			24-hour TSP - 1 time
Impact AQM			Impact AQM			Impact AQM
21-Jun	22-Jun		24-Jun			27-Jun
		1-hour TSP - 3 times			1-hour TSP - 3 times	
		24-hour TSP - 1 time			24-hour TSP - 1 time	
		Impact AQM			Impact AQM	
28-Jun	29-Jun				Impact AQW	
20 0011	1-hour TSP - 3 times	00 0di1				
	24-hour TSP - 1 time					
	Impact AQM					

HY/2012/08 - Tuen Mun - Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section Air Quality Impact Monitoring Schedule - July 2015

Air quality monitoring stations: ASR1, ASR5, ASR6, ASR10, AQMS1

1-hour TSP - 3 times	All quality monitoring static	ONS: ASR1, ASR5, ASR6, A I	I AGINOT				
Public Holiday 01-Jul 02-Jul 03-Jul 04-Jul 04-J							
Public Holiday 01-Jul 02-Jul 03-Jul 04-Jul 04-J							
1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour	Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
A-hour TSP - 1 time				Public Holiday 01-Jul	02-Jul	03-Jul	04-Jul
Impact AQM					1-hour TSP - 3 times		
1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 3					24-hour TSP - 1 time		
1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 3							
1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP - 3 times 24-hour TSP - 3							
1-hour TSP - 3 times 24-hour TSP - 1 time Impact AQM Impact AQM 12-Jul 13-Jul 14-Jul 15-Jul 16-Jul 17-Jul 18-Jul 1-hour TSP - 3 times 24-hour TSP - 1 time Impact AQM 1-hour TSP - 3 times 24-hour TSP - 3 times 24-hour TSP - 1 time Impact AQM							
24-hour TSP - 1 time Impact AQM Impact AQM Impact AQM Impact AQM 16-Jul 17-Jul 18-Jul 1		06-Jul		08-Jul	09-Jul		11-Jul
Impact AQM							
12-Jul 13-Jul 14-Jul 15-Jul 16-Jul 17-Jul 18-Jul 1	24-hour TSP - 1 time		24-hour TSP - 1 time			24-hour TSP - 1 time	
12-Jul 13-Jul 14-Jul 15-Jul 16-Jul 17-Jul 18-Jul 1							
12-Jul 13-Jul 14-Jul 15-Jul 16-Jul 17-Jul 18-Jul 1							
1-hour TSP - 3 times		40.1.1			10.1.1		10.1.1
Marcia M	12-Jul		14-Jul	15-Jul		17-Jul	18-Jul
Impact AQM Impact AQM Impact AQM Impact AQM Impact AQM 23-Jul 24-Jul 25-Jul 25-Jul 1-hour TSP - 3 times 24-hour TSP - 1 time Impact AQM Impact AQM Impact AQM Impact AQM Impact AQM Impact AQM 31-Jul 3							
19-Jul 20-Jul 21-Jul 22-Jul 23-Jul 24-Jul 25-Jul 25-Jul 1-hour TSP - 3 times 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP		24-hour TSP - 1 time			24-hour TSP - 1 time		
19-Jul 20-Jul 21-Jul 22-Jul 23-Jul 24-Jul 25-Jul 25-Jul 1-hour TSP - 3 times 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP							
19-Jul 20-Jul 21-Jul 22-Jul 23-Jul 24-Jul 25-Jul 25-Jul 1-hour TSP - 3 times 1-hour TSP - 3 times 24-hour TSP - 1 time 1-hour TSP		Lanca and A O N 4			Lanca and A ONA		
1-hour TSP - 3 times 24-hour TSP - 1 time Impact AQM 26-Jul			21 Jul			24 Jul	25 Jul
24-hour TSP - 1 time Impact AQM Impact AQM Impact AQM Impact AQM 26-Jul 27-Jul 28-Jul 29-Jul 30-Jul 31-Jul		20-Jul	21-301		23-Jul	24-Jul	
Impact AQM Impact AQM Impact AQM Impact AQM Impact AQM Impact AQM 30-Jul 31-Jul 31-Jul<							
26-Jul 27-Jul 28-Jul 29-Jul 30-Jul 31-Jul	24-11001 TSF - 1 tillle			24-11001 13F - 1 tillle			24-11001 13F - 1 tillle
26-Jul 27-Jul 28-Jul 29-Jul 30-Jul 31-Jul							
26-Jul 27-Jul 28-Jul 29-Jul 30-Jul 31-Jul	Impact AOM			Impact AOM			Impact AOM
		27- Jul			30-Jul	31-Jul	
11-1000 FOE - 3 10068 - 1	20-001	21-0di	1-hour TSP - 3 times	25-001		1-hour TSP - 3 times	
24-hour TSP - 1 time							
Impact AQM			Impact AQM			Impact AQM	

HY/2012/08 - Tuen Mun - Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section Air Quality Impact Monitoring Schedule - August 2015

Air quality monitoring stations: ASR1, ASR5, ASR6, ASR10, AQMS1

Air quality monitoring station	ons: ASR1, ASR5, ASR6, A	ASR10, AQMS1				
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						01-Aug
02-Aug	03-Aug	04-Aug	05-Aug	06-Aug	07-Aug	08-Aug
<u> </u>	1-hour TSP - 3 times	0 . <i>1</i>	00 7 10 9	1-hour TSP - 3 times	0. 7.u.g	00 / 10 g
	24-hour TSP - 1 time			24-hour TSP - 1 time		
00 4	Impact AQM	11 0	10 10	Impact AQM	44 0	45 Aug
09-Aug 1-hour TSP - 3 times	10-Aug	11-Aug	12-Aug 1-hour TSP - 3 times	13-Aug	14-Aug	15-Aug 1-hour TSP - 3 times
24-hour TSP - 1 time			24-hour TSP - 1 time			24-hour TSP - 1 time
21 Hour For Tumo			21 Hour For Tunio			2 modi roi rumo
Impact AQM	47 4	40 4	Impact AQM	00.4	04 4	Impact AQM
16-Aug	17-Aug	18-Aug 1-hour TSP - 3 times	19-Aug	20-Aug	21-Aug 1-hour TSP - 3 times	22-Aug
		24-hour TSP - 1 time			24-hour TSP - 1 time	
		Impact AQM			Impact AQM	
23-Aug		25-Aug	26-Aug	27-Aug	28-Aug	29-Aug
	1-hour TSP - 3 times			1-hour TSP - 3 times		
	24-hour TSP - 1 time			24-hour TSP - 1 time		
	Impact AQM			Impact AQM		
30-Aug				Impact AQIII		
1-hour TSP - 3 times	017.09					
24-hour TSP - 1 time						
Impact AQM						
πηρασι Αφινί				<u>l</u>		<u>l</u>

HY/2012/08 - Tuen Mun - Chek Lap Kok Link - Northern Connection Sub-sea Tunnel Section Impact Marine Water Quality Monitoring (WQM) Schedule (June 15)

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	01-Jun	02-Jun	03-Jun	04-Jun	05-Jun	06-Jun
	WQM Mid-Ebb		WQM Mid-Ebb		WQM Mid-Flood	
	12:17		13:29		7:54	
	(10:32 - 14:02)		(11:44 - 15:14)		(06:09 - 09:39)	
	Mid-Flood		Mid-Flood		Mid-Ebb	
	19:03		20:28		14:50	
	(17:18 - 20:48)		(18:43 - 22:13)		(13:05 - 16:35)	
07-Ju	ın 08-Jun	09-Jun	10-Jun	11-Jun	12-Jun	13-Jun
14-Ju	ın 15-Jun	16-Jun	17-Jun	18-Jun	19-Jun	20-Jun
21-Ju	ın 22-Jun	23-Jun	24-Jun	25-Jun	26-Jun	27-Jun
28-Ju	ın 29-Jun	30-Jun				

HY/2012/08 - Tuen Mun - Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section Impact Dolphin Monitoring Survey Monitoring Schedule - June 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	01-Jun		03-Jun	04-Jun	05-Jun	06-Jun
		Impact Dolphin Monitoring				
07-Jun	08-Jun	09-Jun	10-Jun	11-Jun	12-Jun	13-Jun
			Impact Dolphin Monitoring			
14-Jun	15-Jun	16-Jun	17-Jun	18-Jun	19-Jun	public holiday 20-Jun
21-Jun	22-Jun	23-Jun	24-Jun	25-Jun	26-Jun	27-Jun
			Impact Dolphin Monitoring		Impact Dolphin Monitoring	
28-Jun	29-Jun	30-Jun				

HY/2012/08 - Tuen Mun - Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section Impact Dolphin Monitoring Survey Monitoring Schedule - July 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
			public holiday 01-Jul		03-Jul	04-Jul
				Impact Dolphin Monitoring		
05-Jul	06-Jul	07-Jul	08-Jul	09-Jul	10-Jul	11-Jul
		Impact Dolphin Monitoring				
12-Jul	13-Jul	14-Jul	15-Jul	16-Jul	17-Jul	18-Jul
40.11						25.1.1
19-Jul	20-Jul		22-Jul Impact Dolphin	23-Jul	24-Jul	25-Jul
			Monitoring			
26-Jul		28-Jul	29-Jul	30-Jul	31-Jul	
	Impact Dolphin Monitoring					

HY/2012/08 - Tuen Mun - Chek Lap Kok Link Northern Connection Sub-sea Tunnel Section Impact Dolphin Monitoring Survey Monitoring Schedule - August 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
						01-Aug
02-Aug	03-Aug	04-Aug	05-Aug	06-Aug	07-Aug	08-Aug
09-Aug	10-Aug Impact Dolphin	11-Aug	12-Aug	13-Aug	14-Aug Impact Dolphin	15-Aug
	Monitoring				Monitoring	
16-Aug	17-Aug	18-Aug		20-Aug	21-Aug	22-Aug
			Impact Dolphin Monitoring			
23-Aug	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug
					Impact Dolphin Monitoring	
30-Aug	31-Aug					

Appendix F

Impact Air Quality Monitoring Results

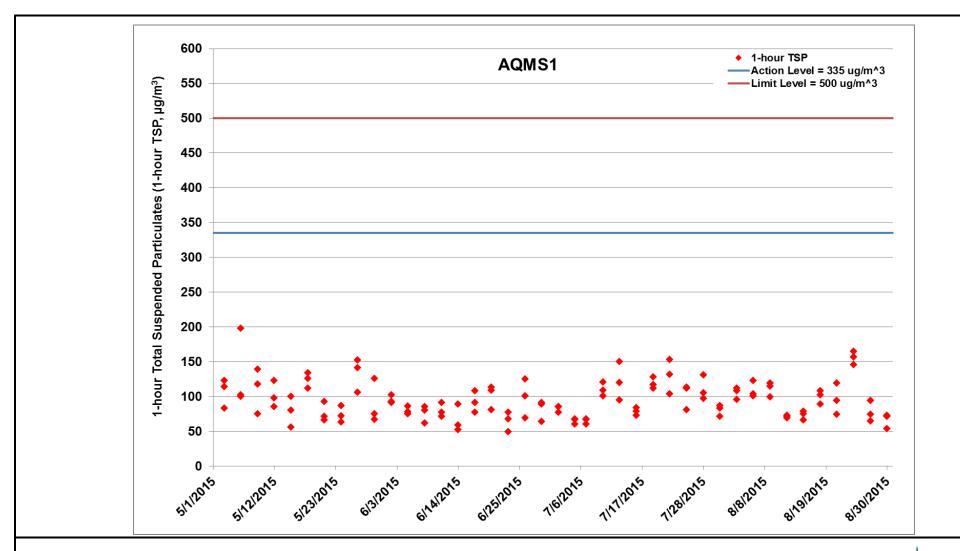


Figure F.1 Impact Monitoring – 1-hour Total Suspended Particulates (μg/m³) at AQMS1 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). *Ref:* 0212330_Impact AQM graphs_August 2015_REV a.xlsx



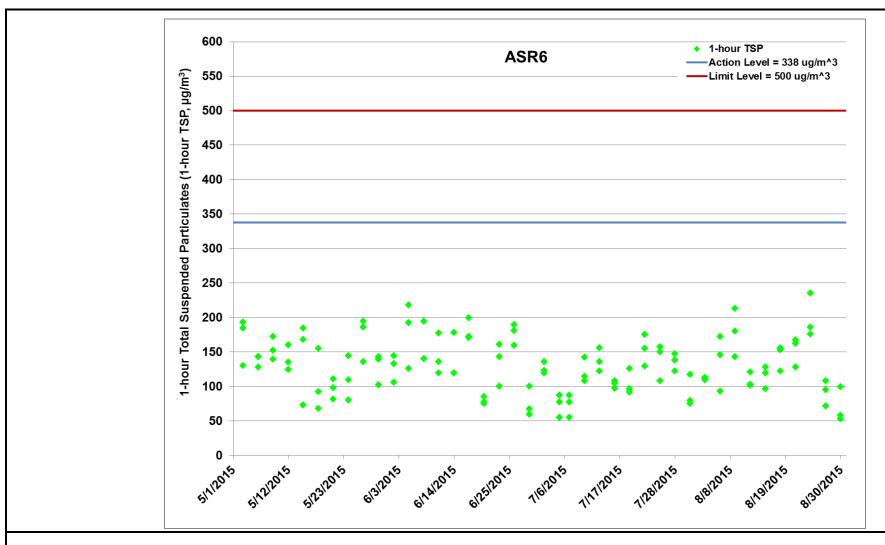


Figure F.2 Impact Monitoring – 1-hour Total Suspended Particulates (μg/m³) at ASR6 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). Ref: 0212330_Impact AQM graphs_August 2015_REV a.xlsx



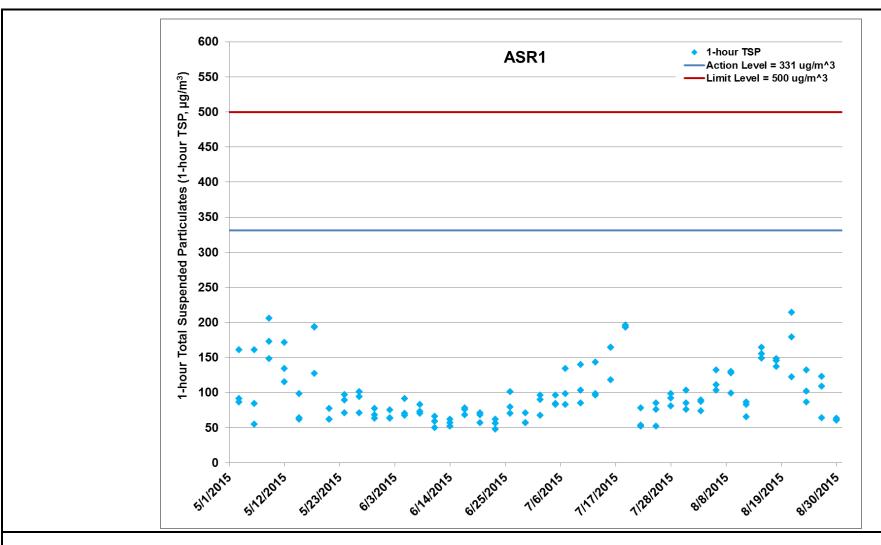


Figure F.3 Impact Monitoring – 1-hour Total Suspended Particulates (μg/m³) at ASR1 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). *Ref*: 0212330_Impact AQM graphs_August 2015_REV a.xlsx



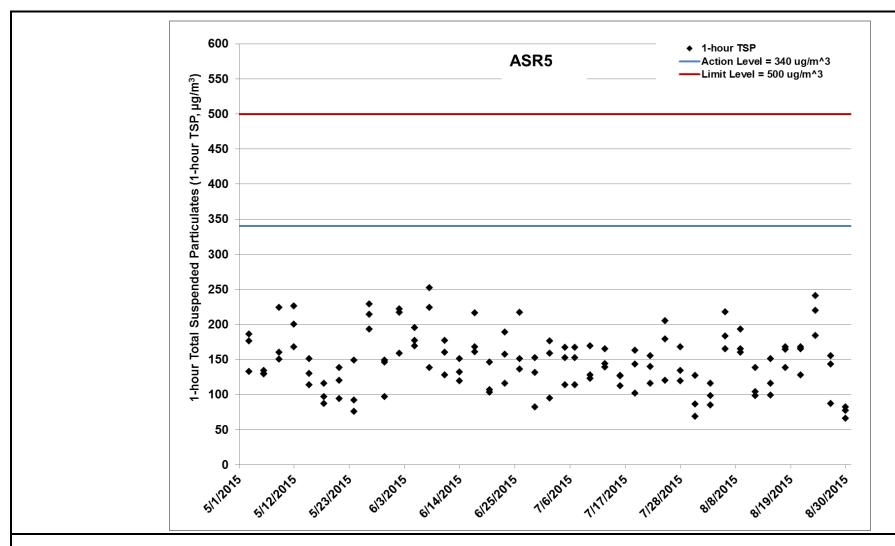


Figure F.4 Impact Monitoring – 1-hour Total Suspended Particulates (μg/m³) at ASR5 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). Ref: 0212330_Impact AQM graphs_August 2015_REV a.xlsx



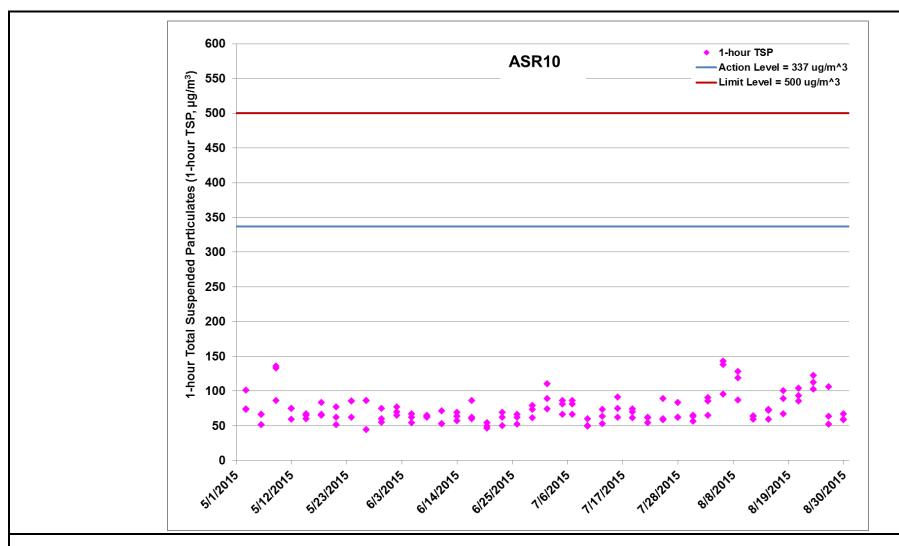


Figure F.5 Impact Monitoring – 1-hour Total Suspended Particulates (μg/m³) at ASR10 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). *Ref:* 0212330_Impact AQM graphs_August 2015_REV a.xlsx



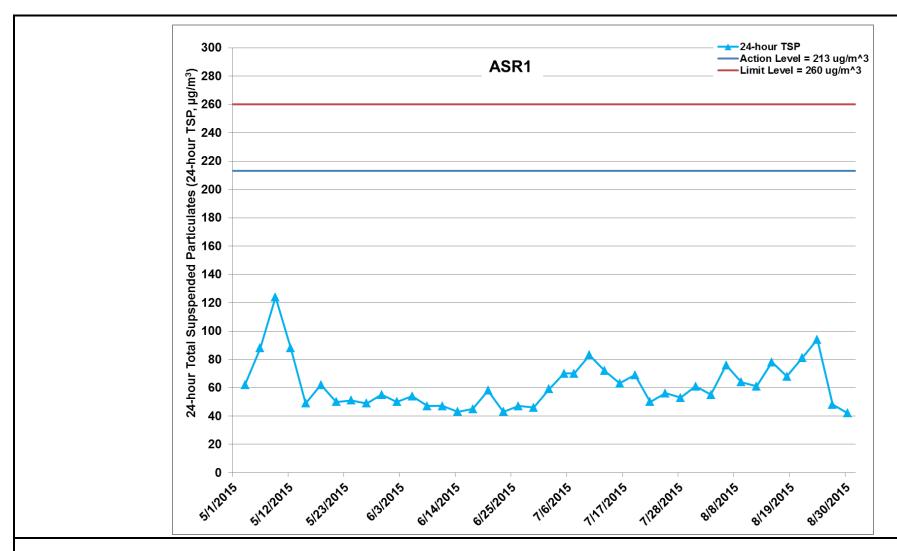


Figure F.6 Impact Monitoring – 24-hour Total Suspended Particulates (μg/m³) at ASR1 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). *Ref:* 0212330_Impact AQM graphs_August 2015_REV a.xlsx



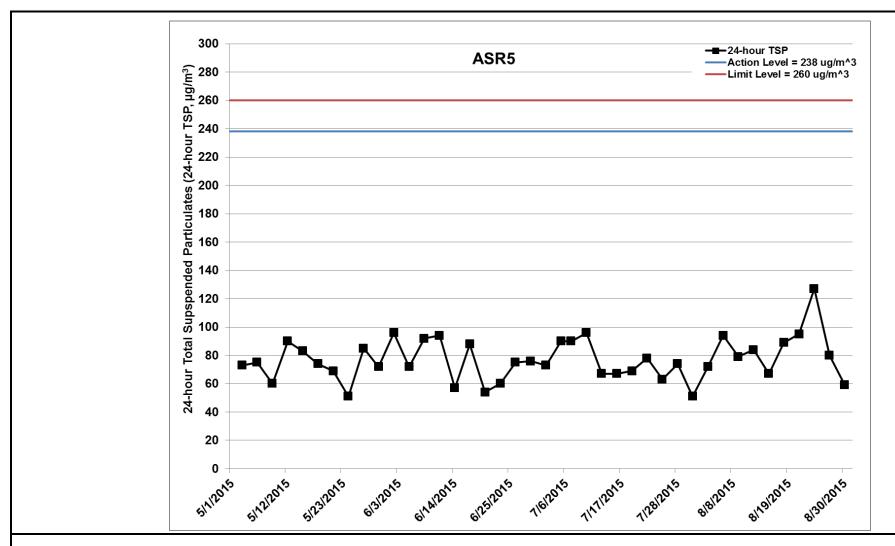


Figure F.7 Impact Monitoring – 24-hour Total Suspended Particulates (μg/m³) at ASR5 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). *Ref:* 0212330_Impact AQM graphs_August 2015_REV a.xlsx



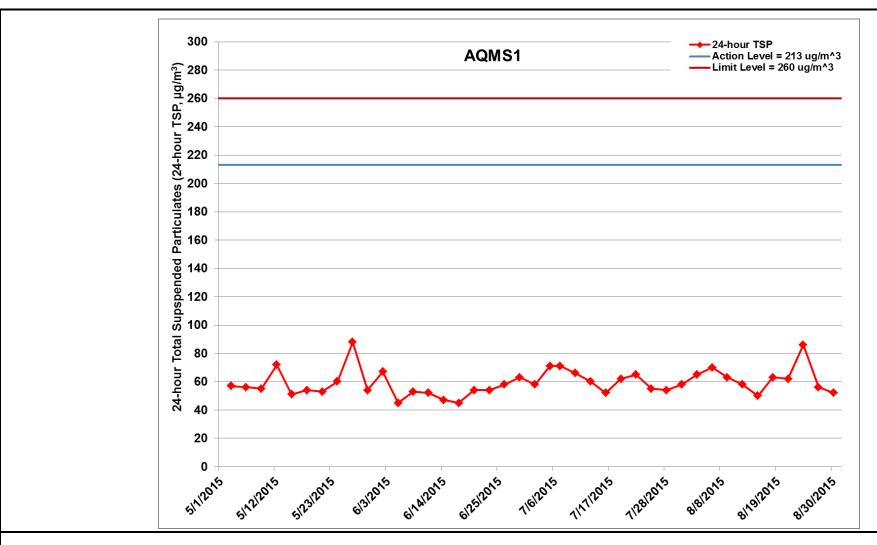


Figure F.8 Impact Monitoring – 24-hour Total Suspended Particulates (μg/m³) at AQMS1 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). *Ref:* 0212330_Impact AQM graphs_August 2015_REV a.xlsx



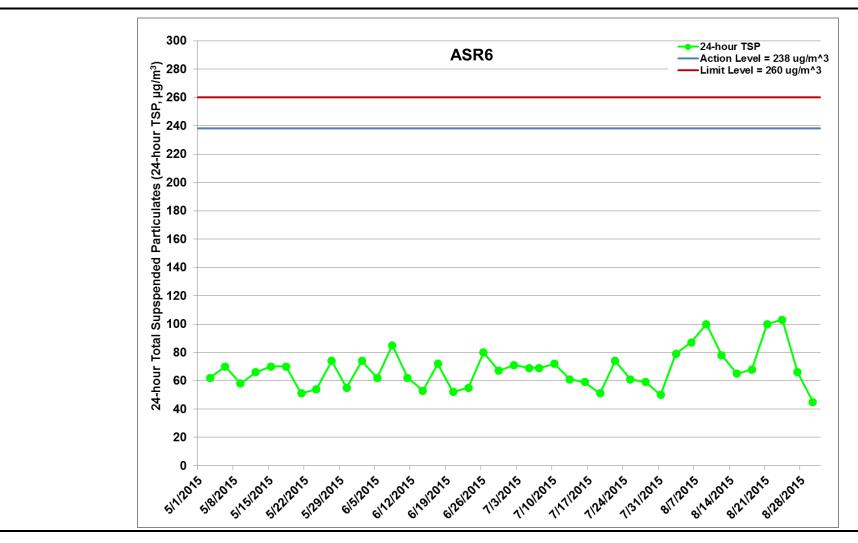


Figure F.9 Impact Monitoring – 24-hour Total Suspended Particulates (μg/m³) at ASR6 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). Ref: 0212330_Impact AQM graphs_August 2015_REV a.xlsx



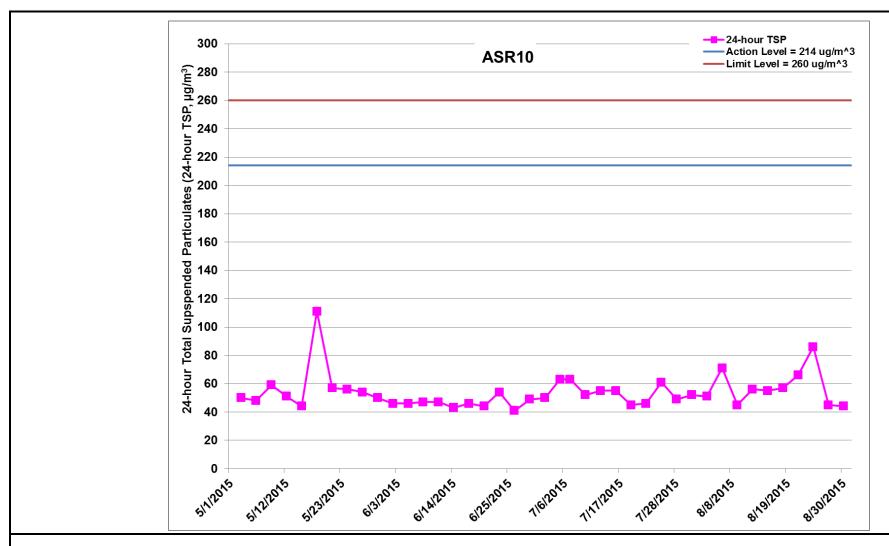


Figure F.10 Impact Monitoring – 24-hour Total Suspended Particulates (μg/m³) at ASR10 between 1 May 2015 and 31 August 2015 during impact monitoring period. The weather conditions during the monitoring period varied from sunny to cloudy. Major land-based construction activities included: Construction of capping beam and base slab for Ventilation Shaft at Works Area – Portion N-C (1/8/2015 – 31/8/2015), Excavation for Ventilation Shaft at Works Area – Portion N-C (1/5/2015 – 31/7/2015) and Setting up of Slurry Treatment Plant (1/5/2015 – 31/7/2015). *Ref:* 0212330_Impact AQM graphs_August 2015_REV a.xlsx



Appendix G

Impact Water Quality Monitoring Results

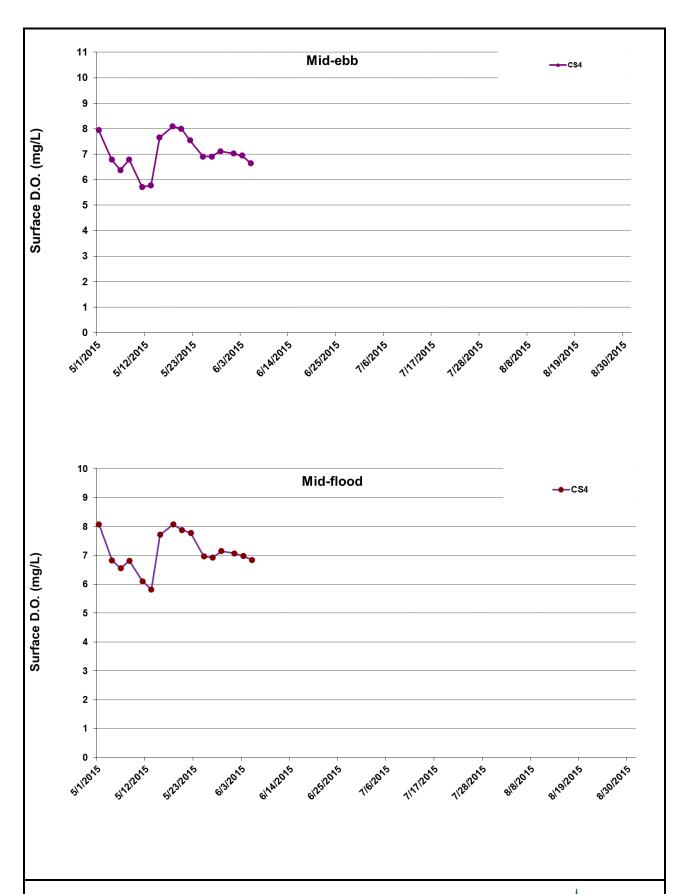


Figure G1 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in surface waters between 1 May 2015 and 5 June 2015 at CS4. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



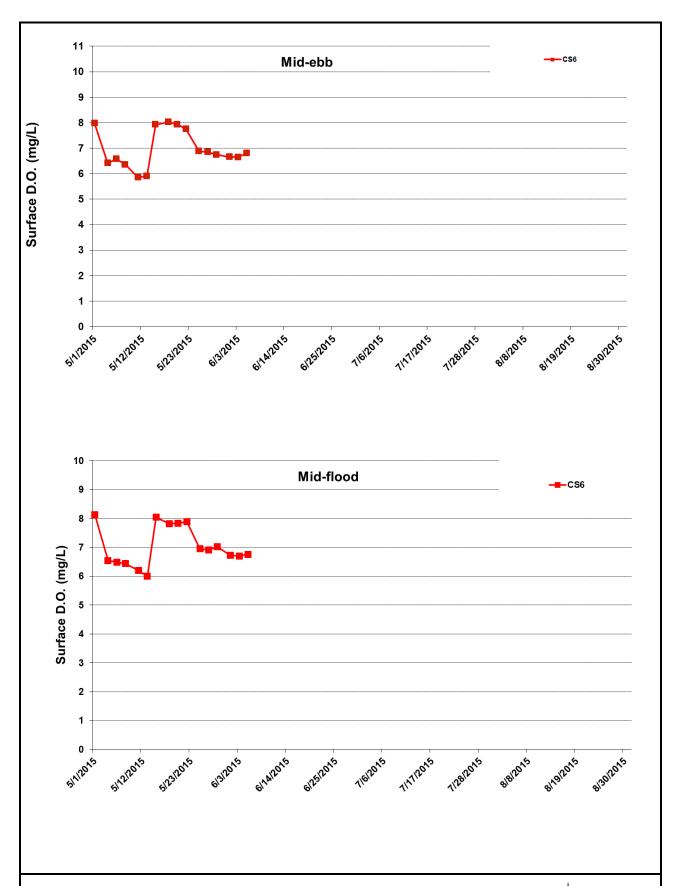


Figure G2 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in surface waters between 1 May 2015 and 5 June 2015 at CS6. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



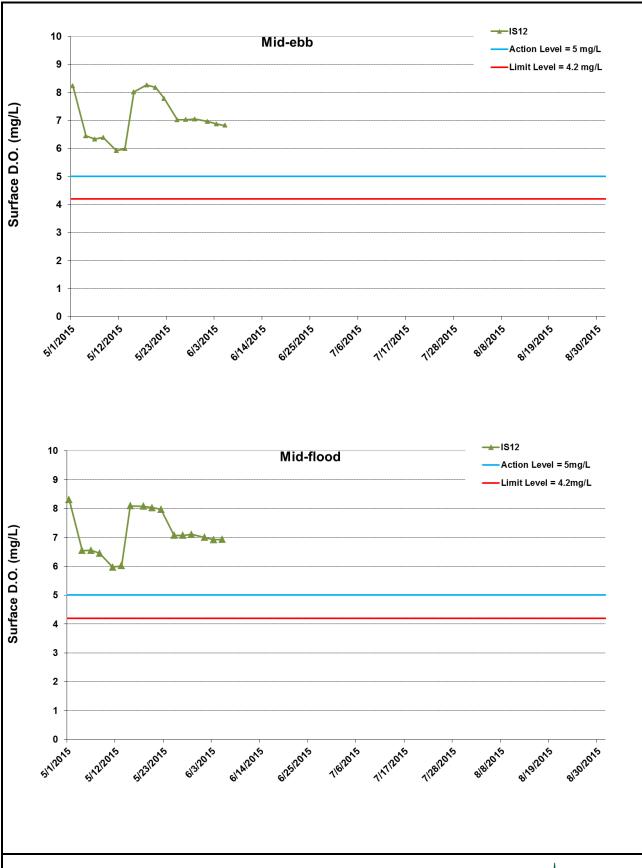


Figure G3 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in surface waters between 1 May 2015 and 5 June 2015 at IS12. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



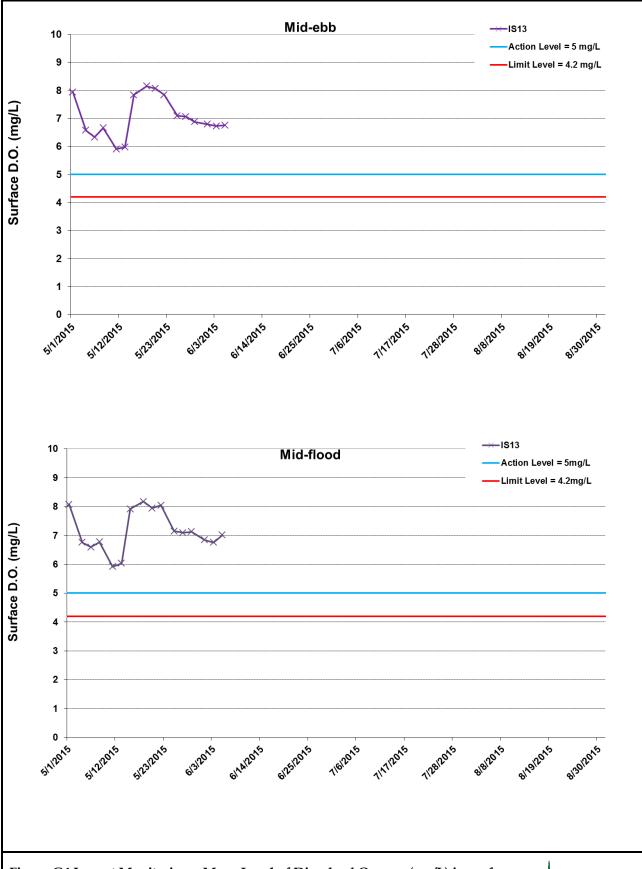


Figure G4 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in surface waters between 1 May 2015 and 5 June 2015 at IS13. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



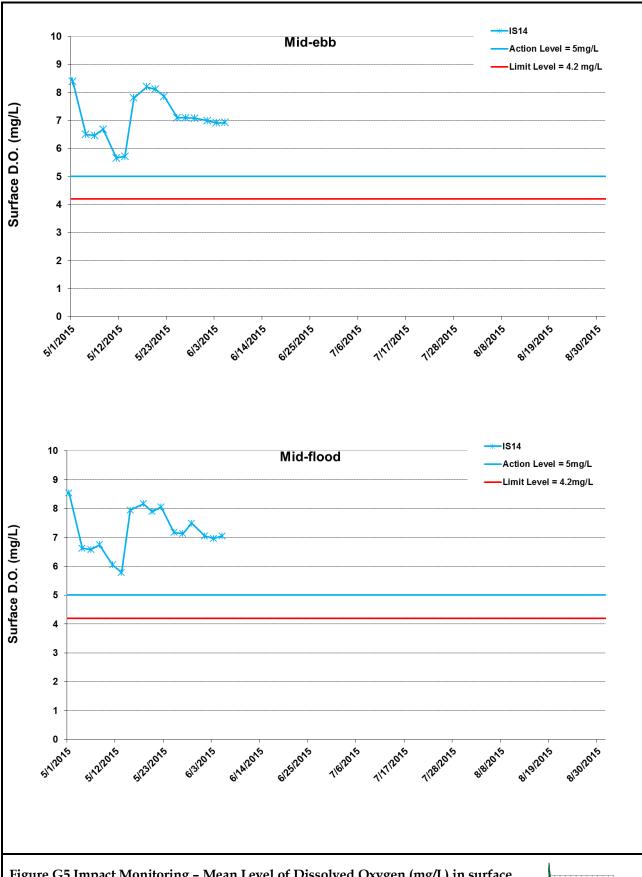


Figure G5 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in surface waters between 1 May 2015 and 5 June 2015 at IS14. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.




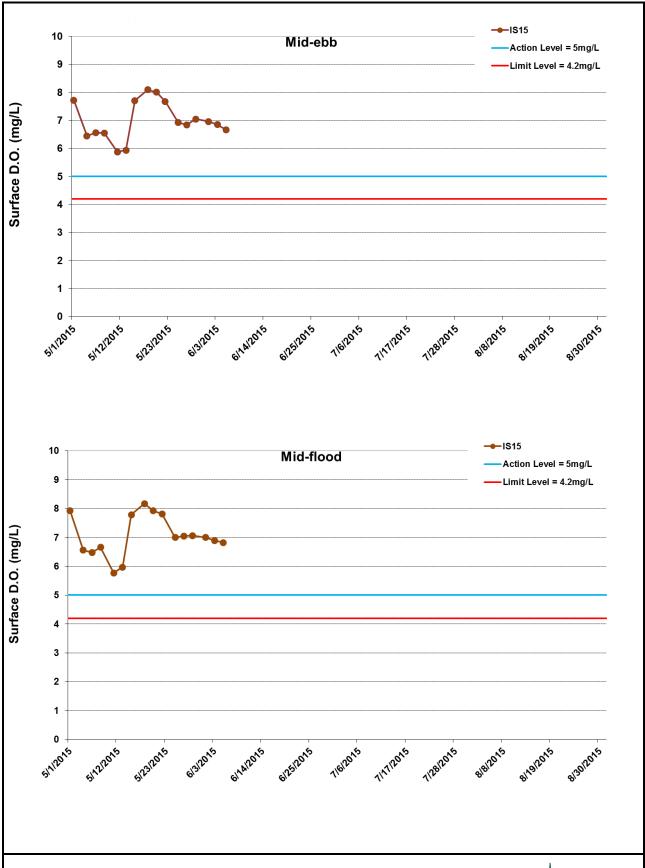


Figure G6 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in surface waters between 1 May 2015 and 5 June 2015 at IS15. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



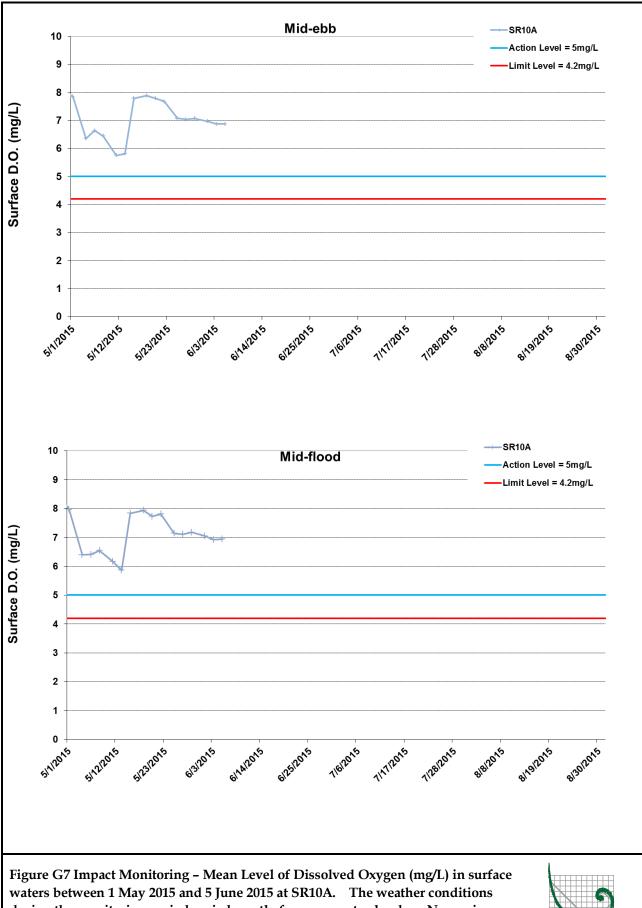

during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



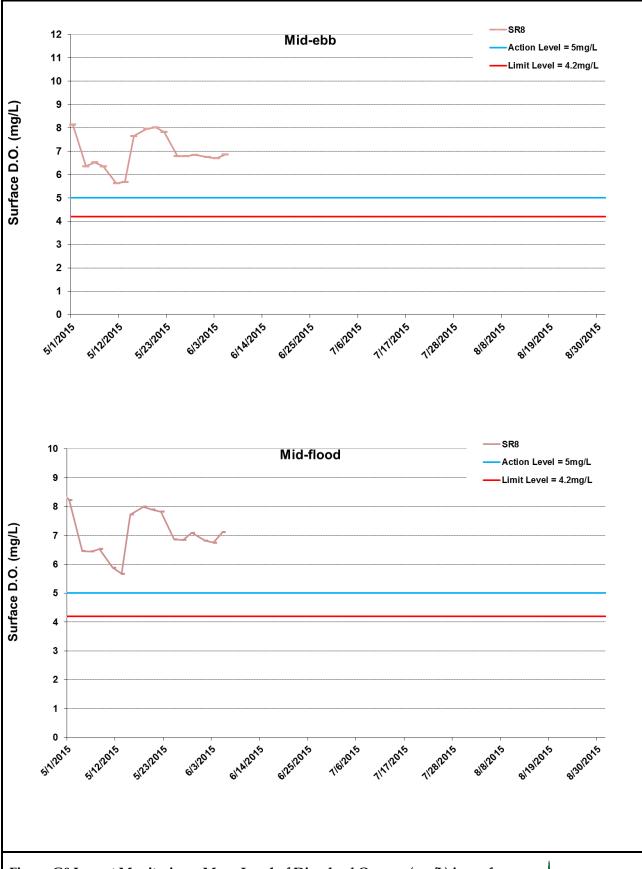


Figure G8 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in surface waters between 1 May 2015 and 5 June 2015 at SR8. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



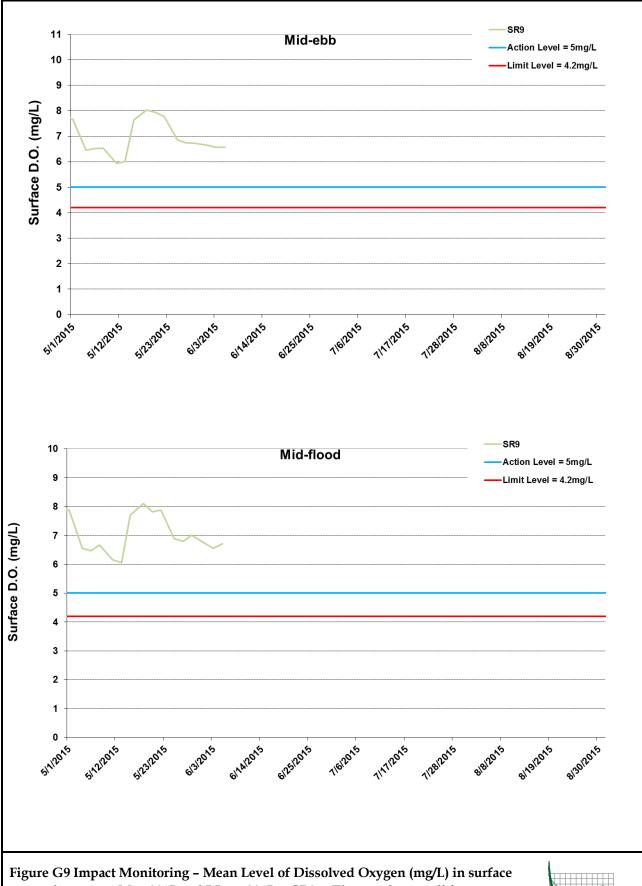


Figure G9 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in surface waters between 1 May 2015 and 5 June 2015 at SR9. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



Ref: 0212330_Impact-WQM_Aug2015_graphs_Rev a.xls

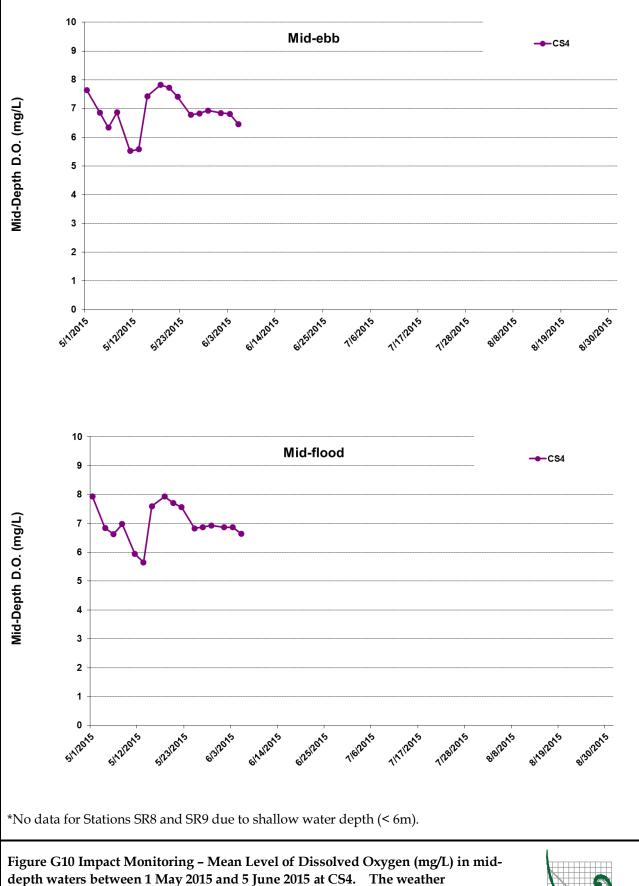


Figure G10 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in middepth waters between 1 May 2015 and 5 June 2015 at CS4. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



Ref: 0212330_Impact-WQM_Aug2015_graphs_Rev a.xls



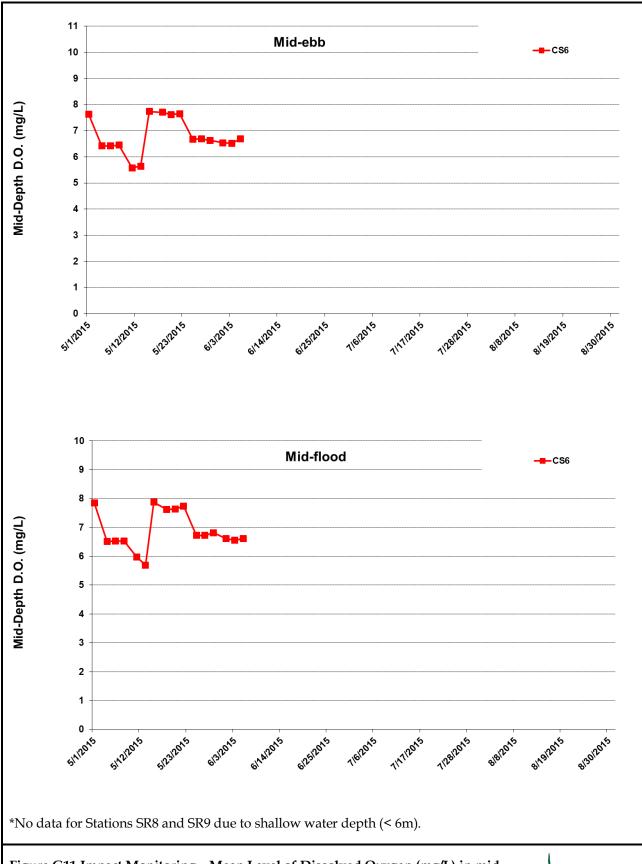


Figure G11 Impact Monitoring - Mean Level of Dissolved Oxygen (mg/L) in middepth waters between 1 May 2015 and 5 June 2015 at CS6. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



Ref: 0212330_Impact-WQM_Aug2015_graphs_Rev a.xls

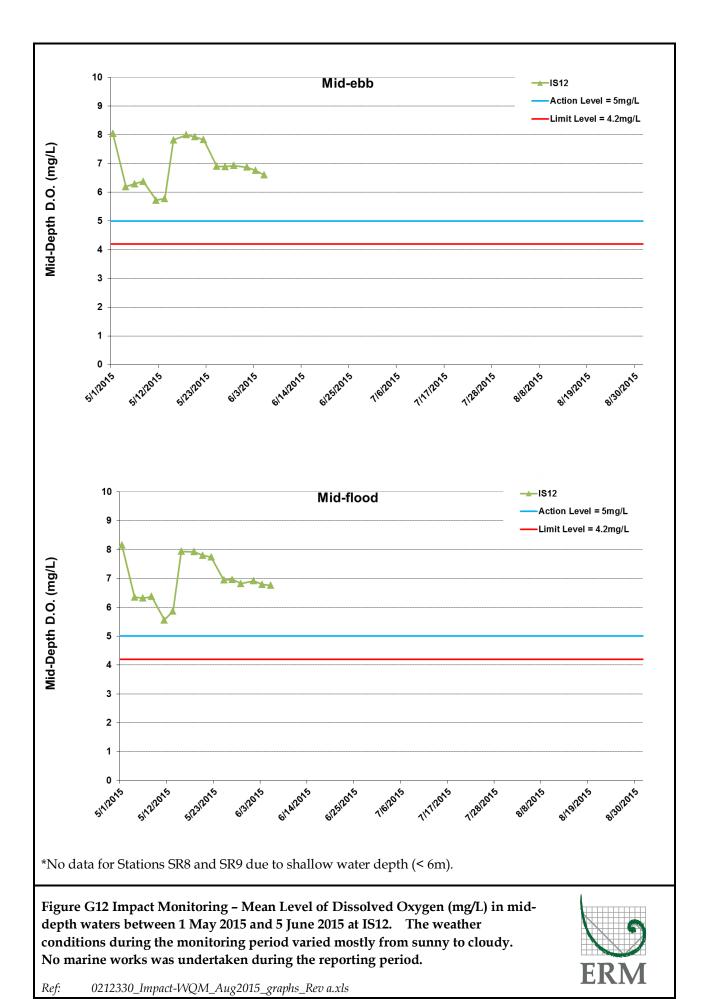


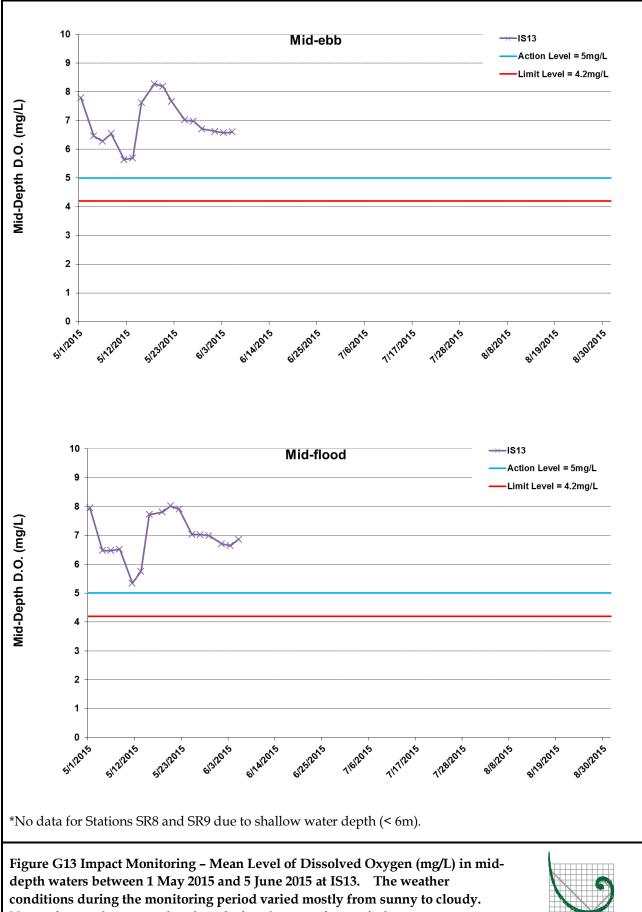

No marine works was undertaken during the reporting period.




Ref: 0212330_Impact-WQM_Aug2015_graphs_Rev a.xls

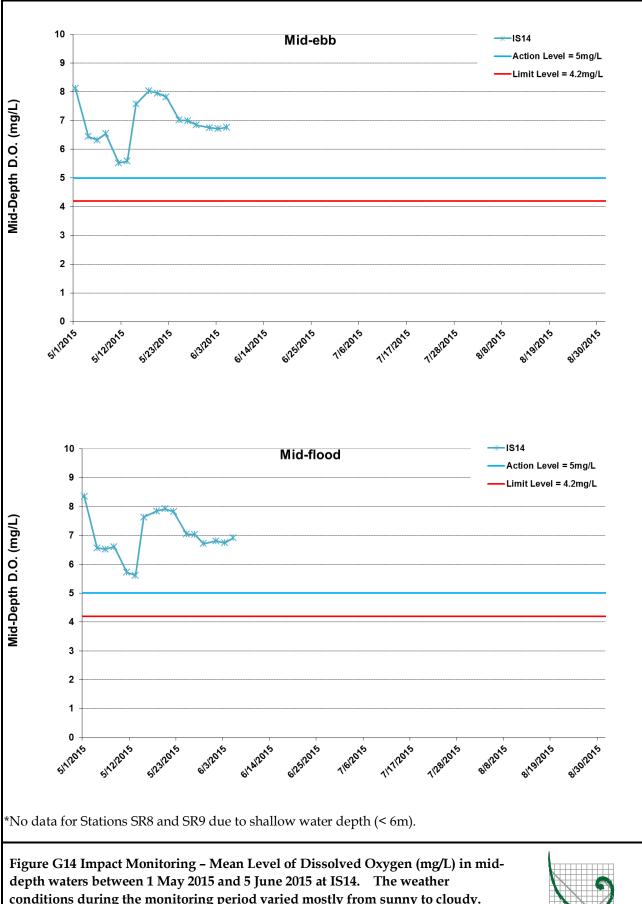

conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.




Ref: 0212330_Impact-WQM_Aug2015_graphs_Rev a.xls

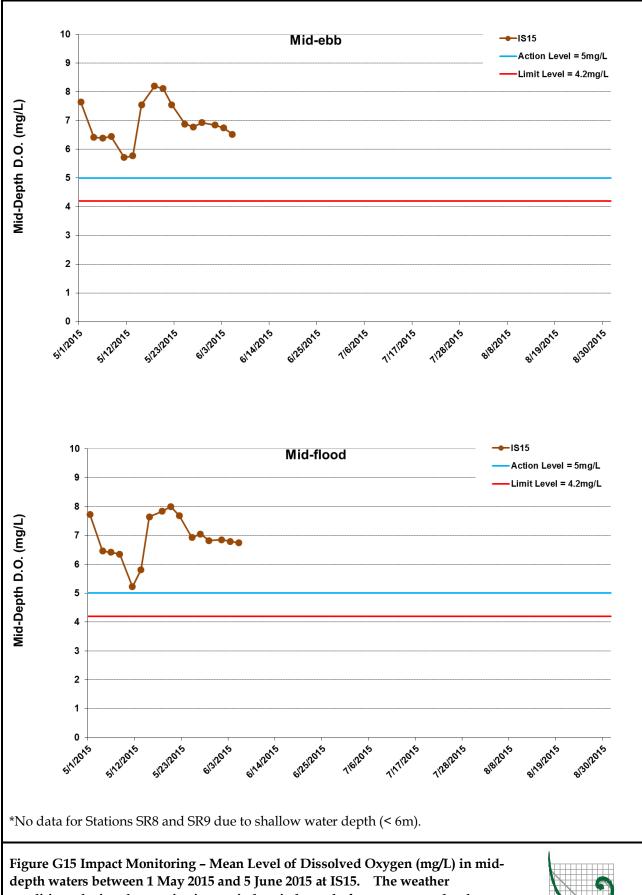

conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



Ref: 0212330_Impact-WQM_Aug2015_graphs_Rev a.xls

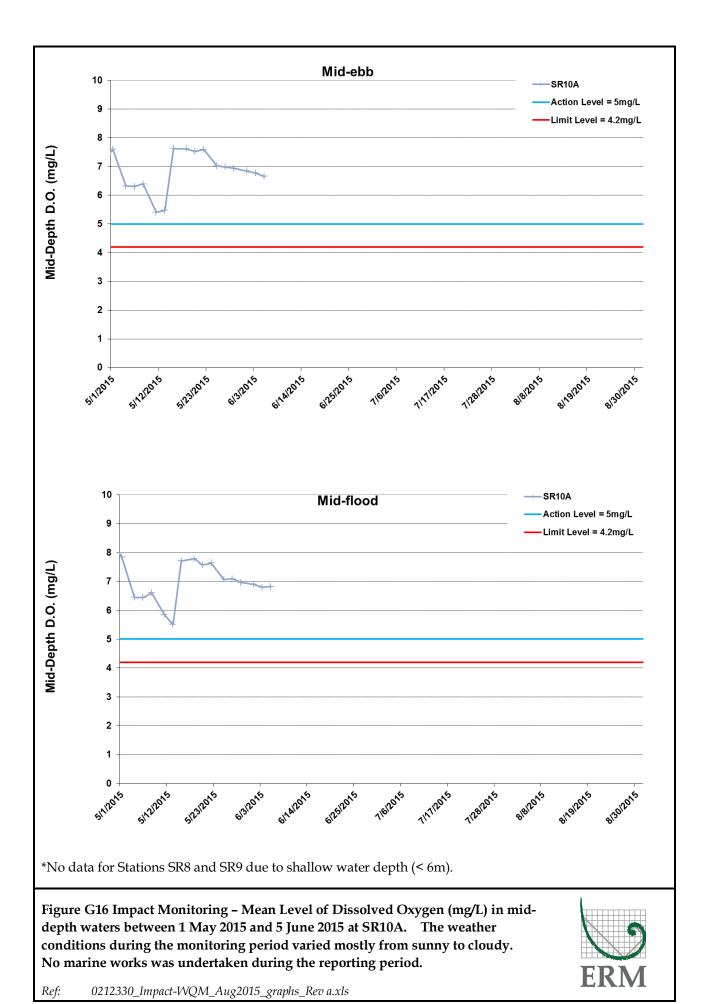

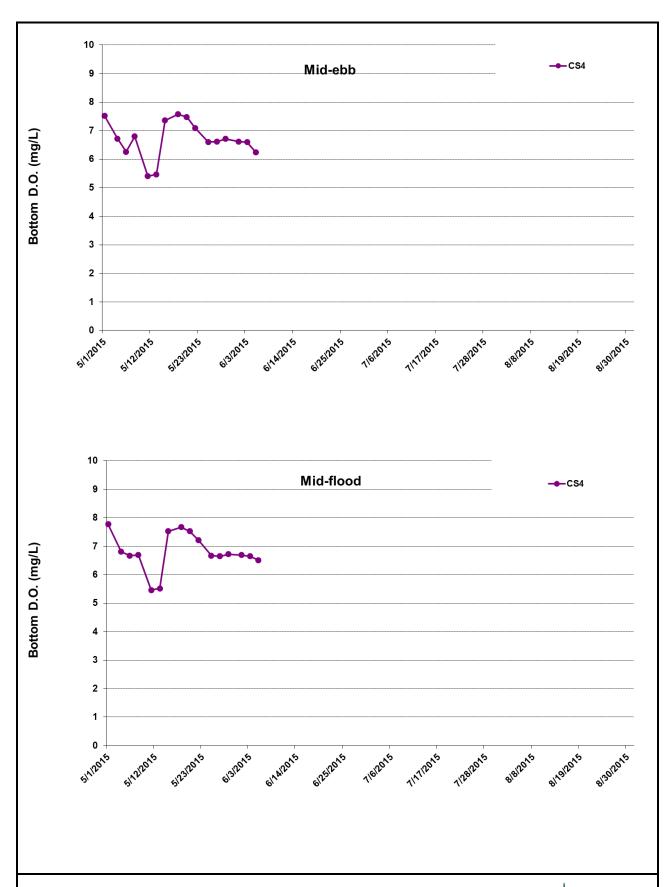


Figure G17 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at CS4. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



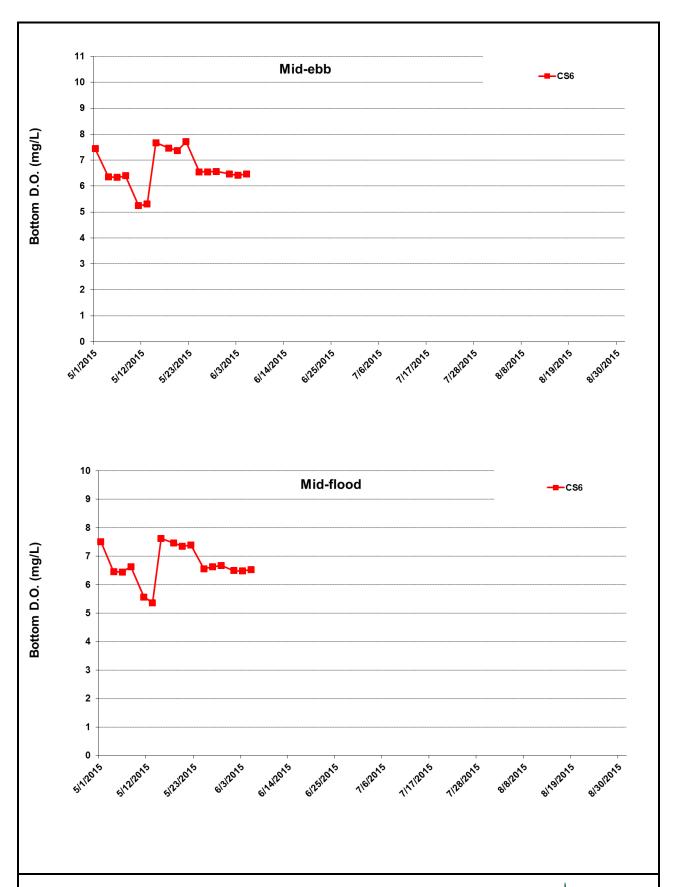


Figure G18 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at CS6. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



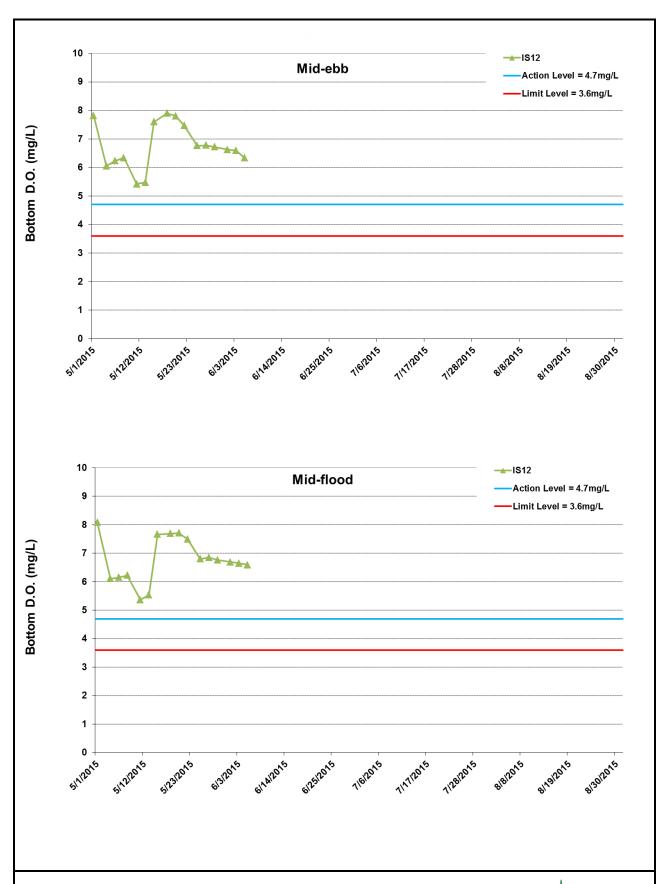


Figure G19 Impact Monitoring - Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at IS12. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



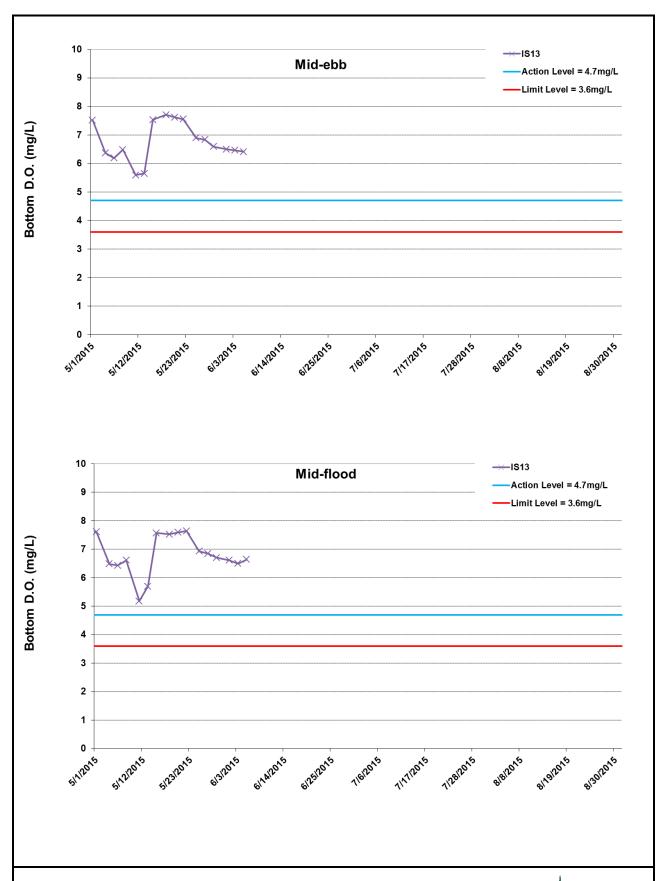


Figure G20 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at IS13. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



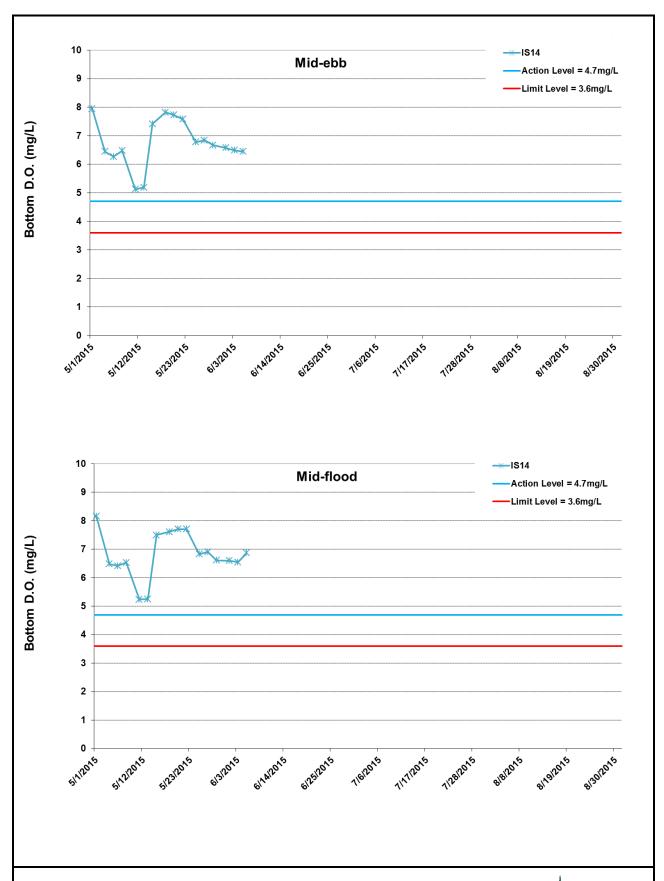


Figure G21 Impact Monitoring - Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at IS14. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



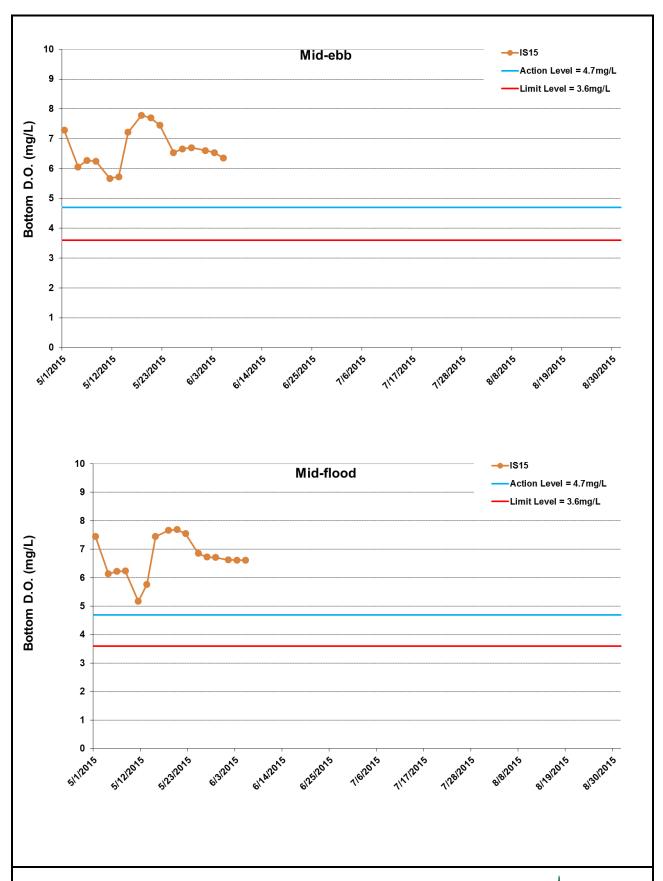


Figure G22 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at IS15. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



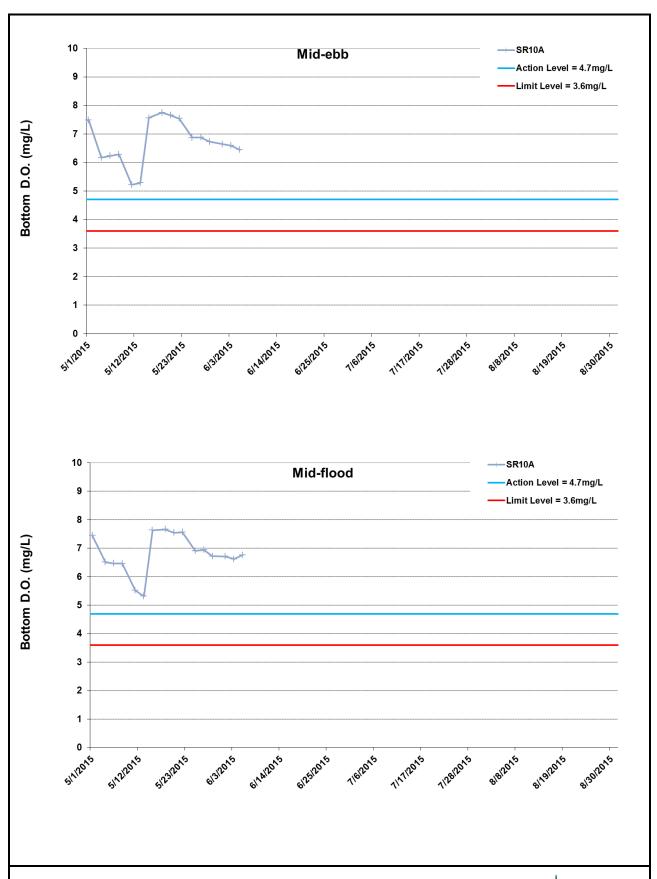


Figure G23 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at SR10A. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



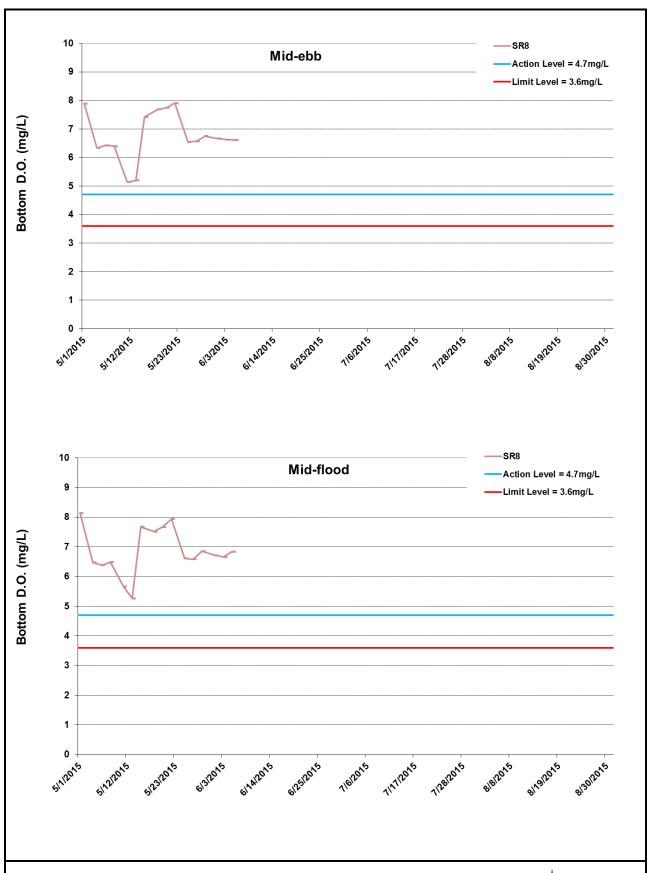


Figure G24 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at SR8. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



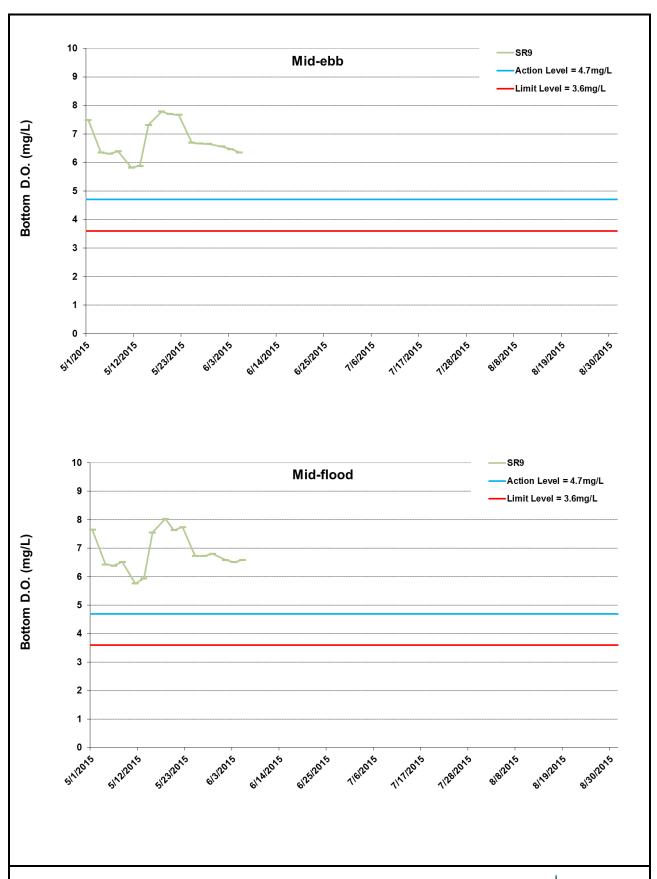


Figure G25 Impact Monitoring – Mean Level of Dissolved Oxygen (mg/L) in bottom water between 1 May 2015 and 5 June 2015 at SR9. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



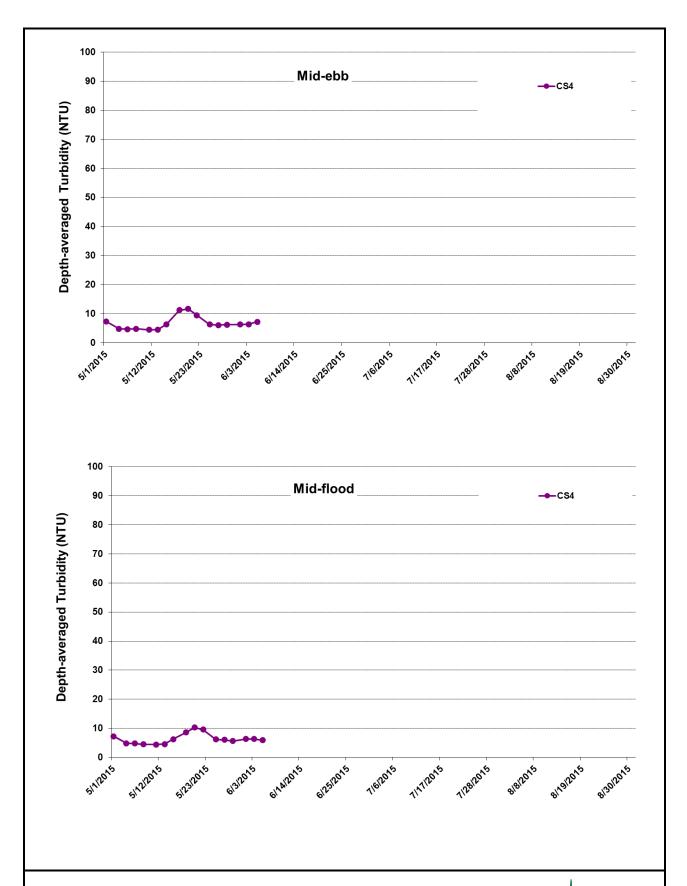


Figure G26 Impact Monitoring – Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at CS4. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



 $Ref: \qquad 0212330_Impact-WQM_Aug2015_graphs_Rev\ a.xls$

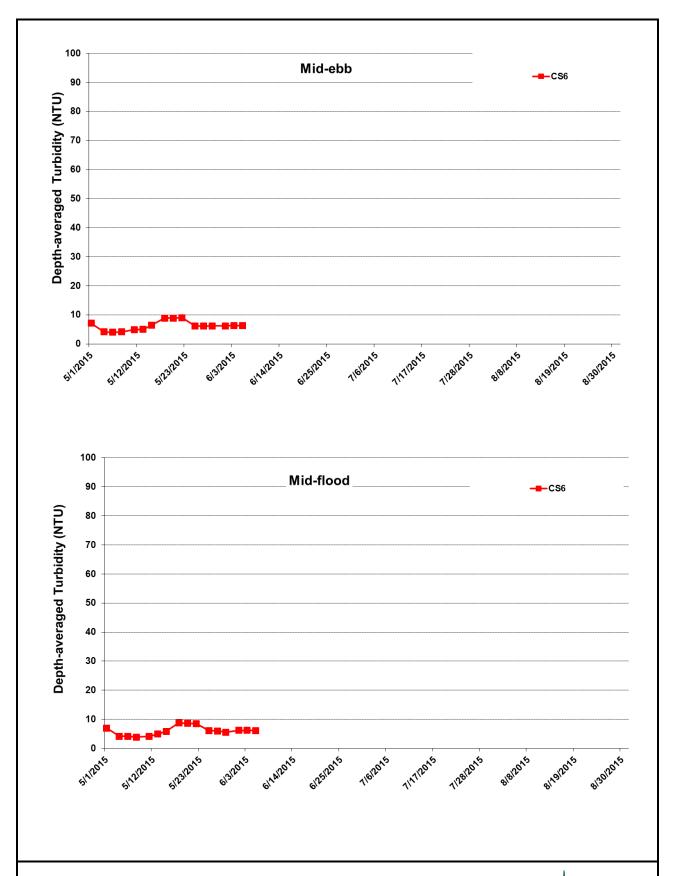


Figure G27 Impact Monitoring – Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at CS6. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



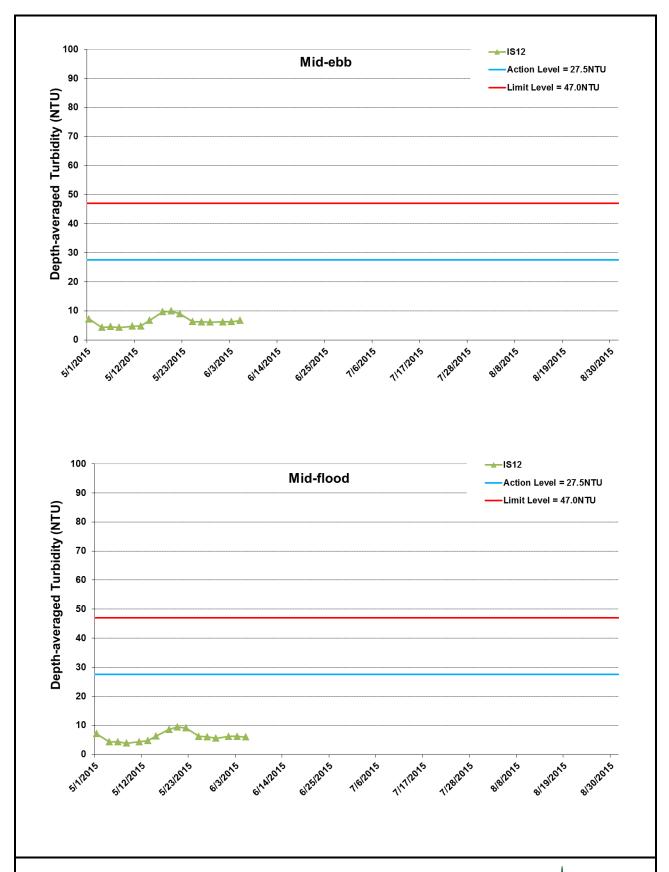


Figure G28 Impact Monitoring – Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at IS12. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



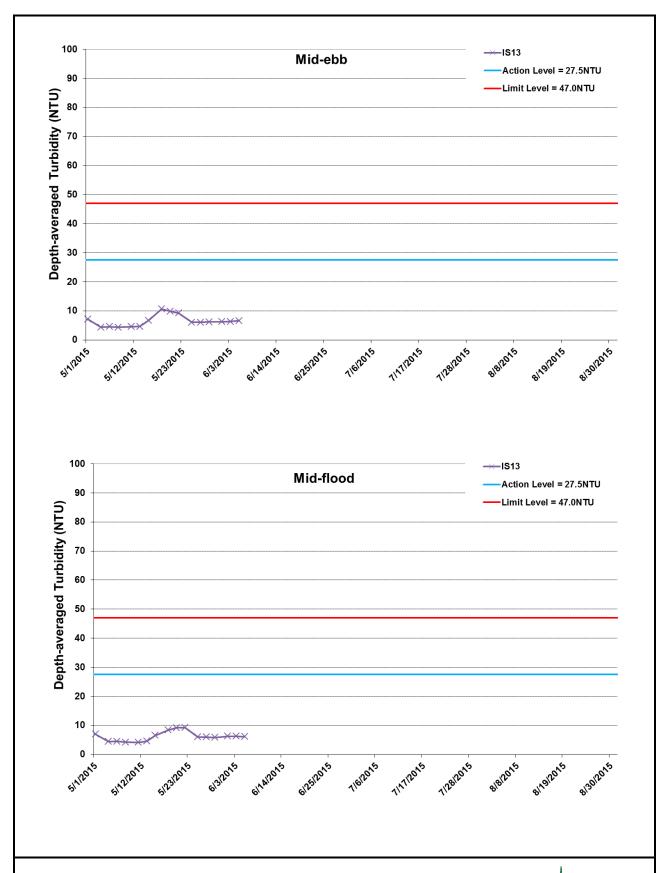


Figure G29 Impact Monitoring – Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at IS13. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



 $Ref: \qquad 0212330_Impact-WQM_Aug2015_graphs_Rev\ a.xls$

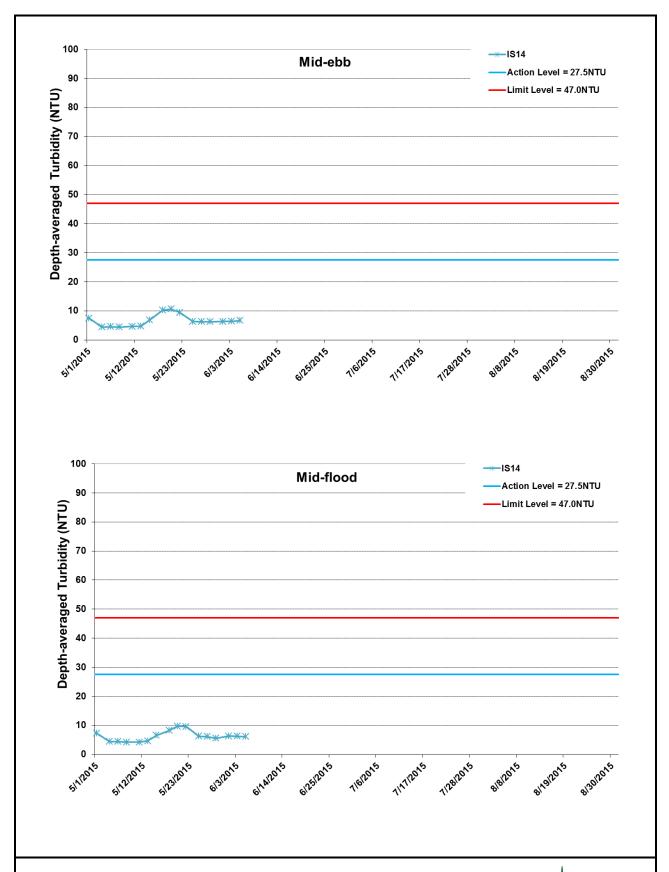


Figure G30 Impact Monitoring – Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at IS14. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



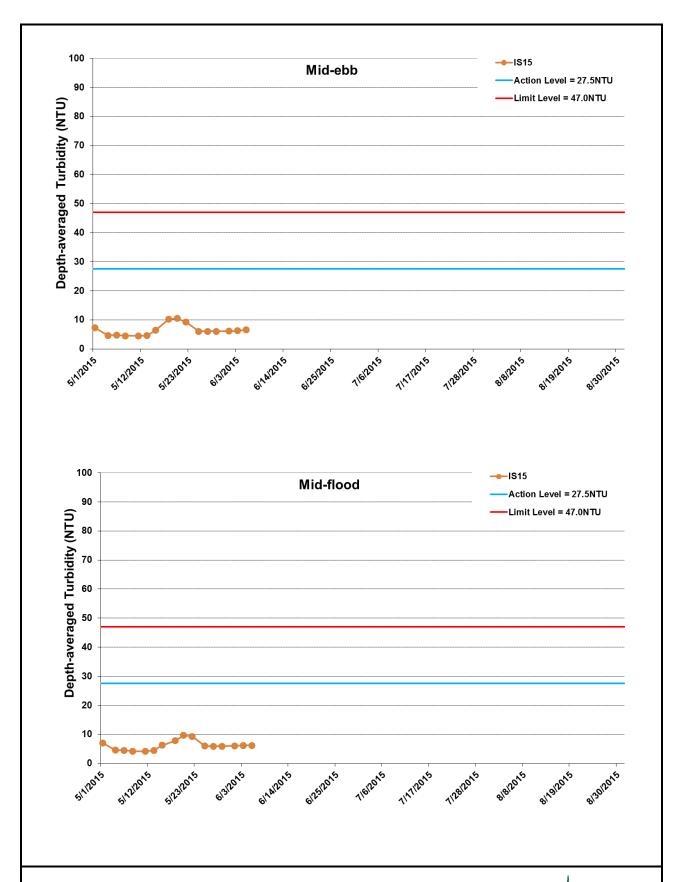


Figure G31 Impact Monitoring - Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at IS15. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



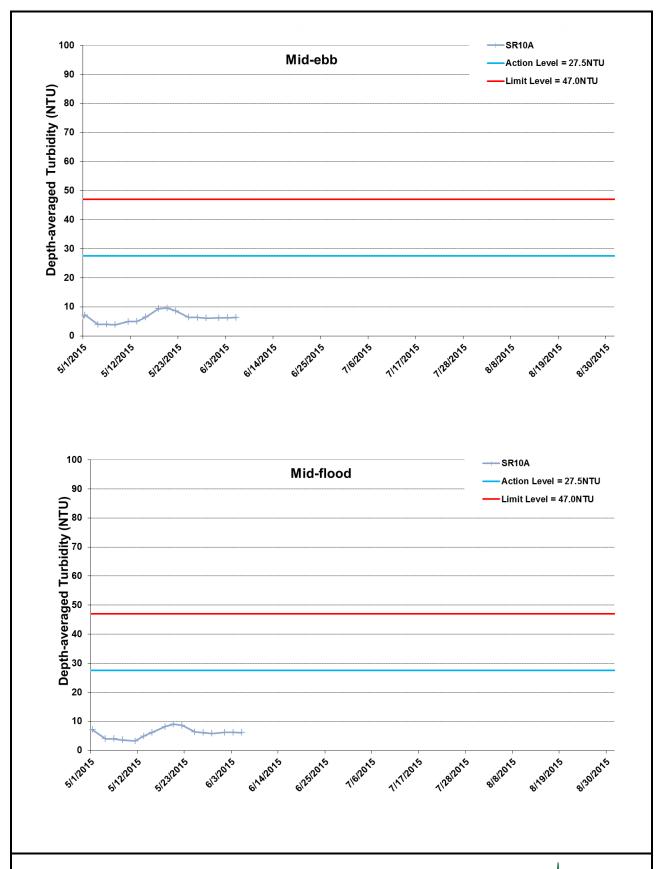


Figure G32 Impact Monitoring - Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at SR10A. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



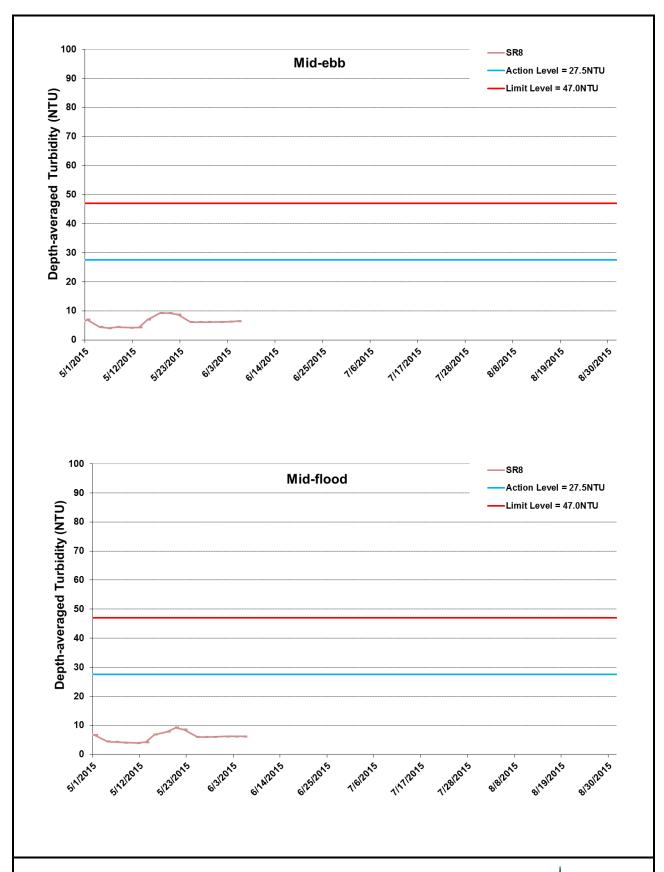


Figure G33 Impact Monitoring - Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at SR8. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



 $Ref: \qquad 0212330_Impact-WQM_Aug2015_graphs_Rev\ a.xls$

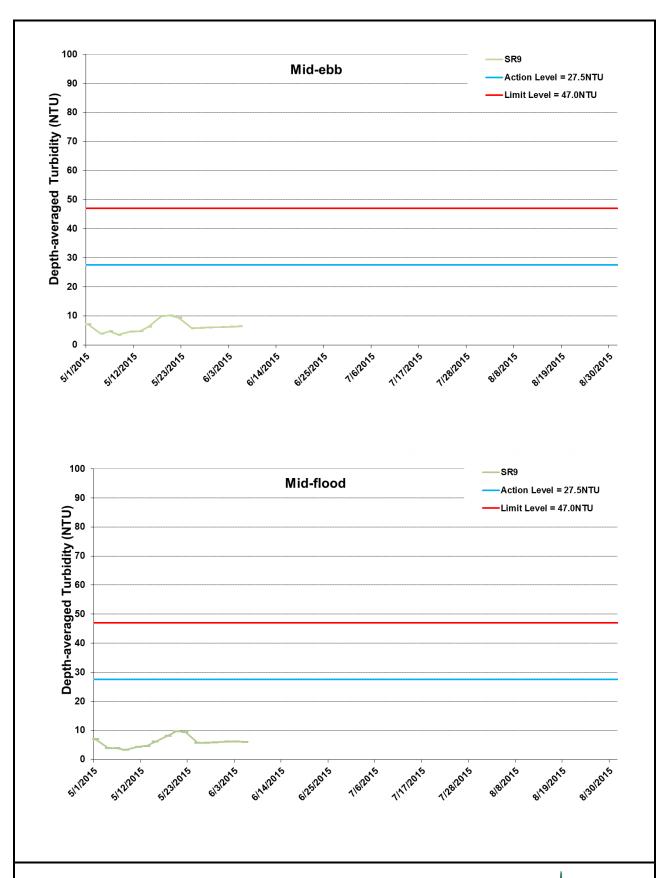


Figure G34 Impact Monitoring - Mean Depth-averaged Level of Turbidity (NTU) between 1 May 2015 and 5 June 2015 at SR9. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



 $Ref: \qquad 0212330_Impact-WQM_Aug2015_graphs_Rev\ a.xls$

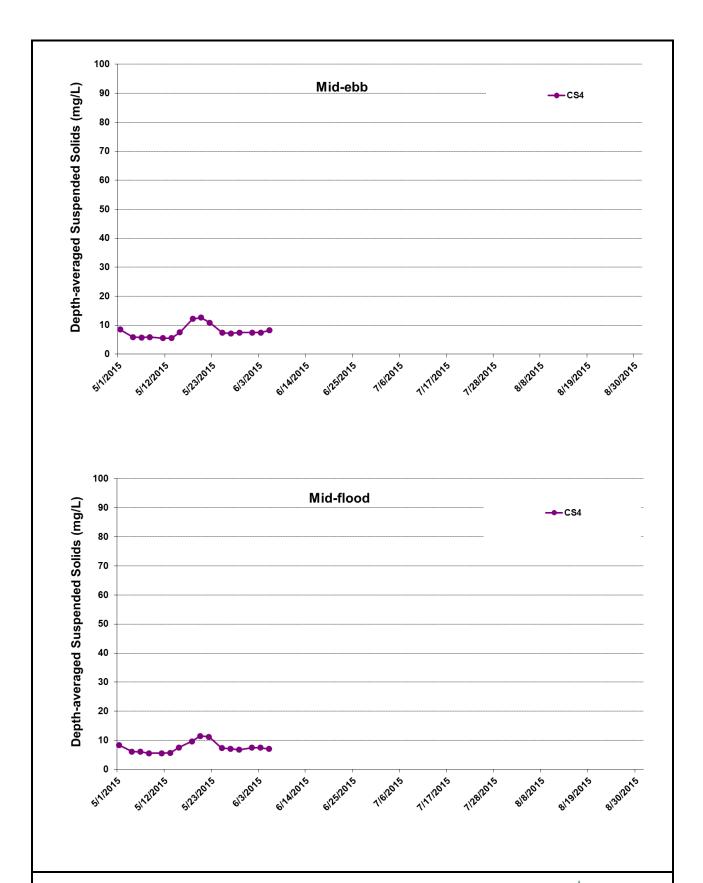


Figure G35 Impact Monitoring – Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at CS4. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



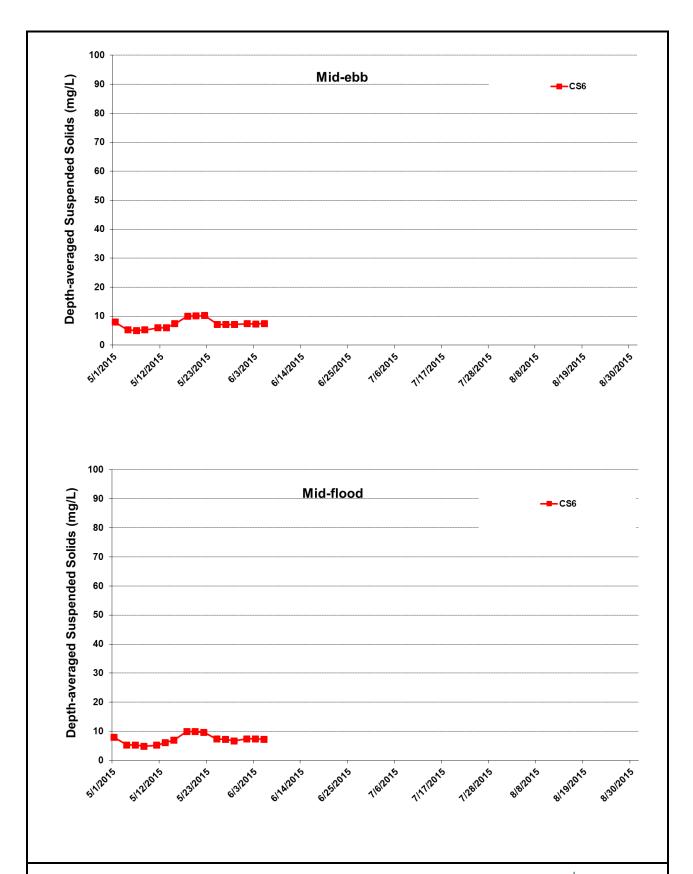


Figure G36 Impact Monitoring – Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at CS6. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



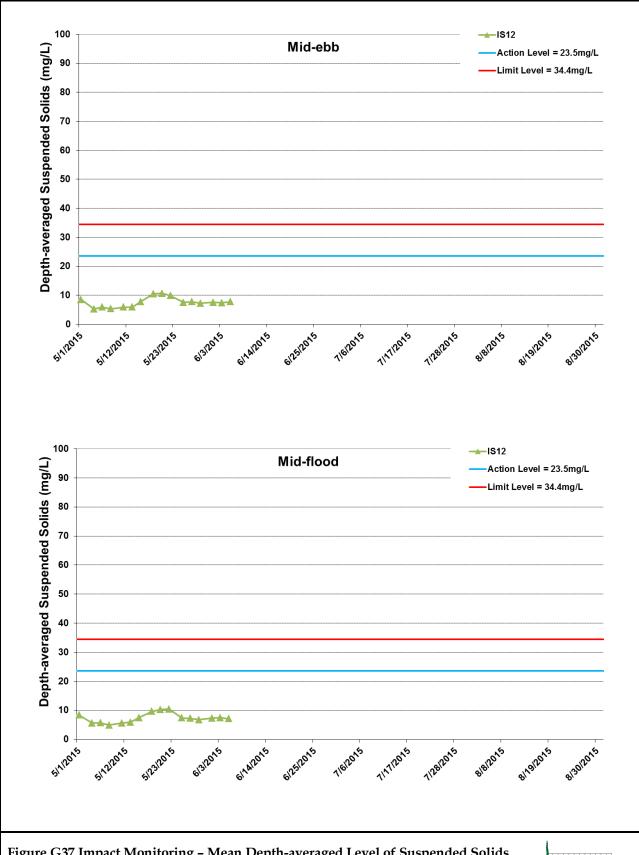


Figure G37 Impact Monitoring – Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at IS12. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



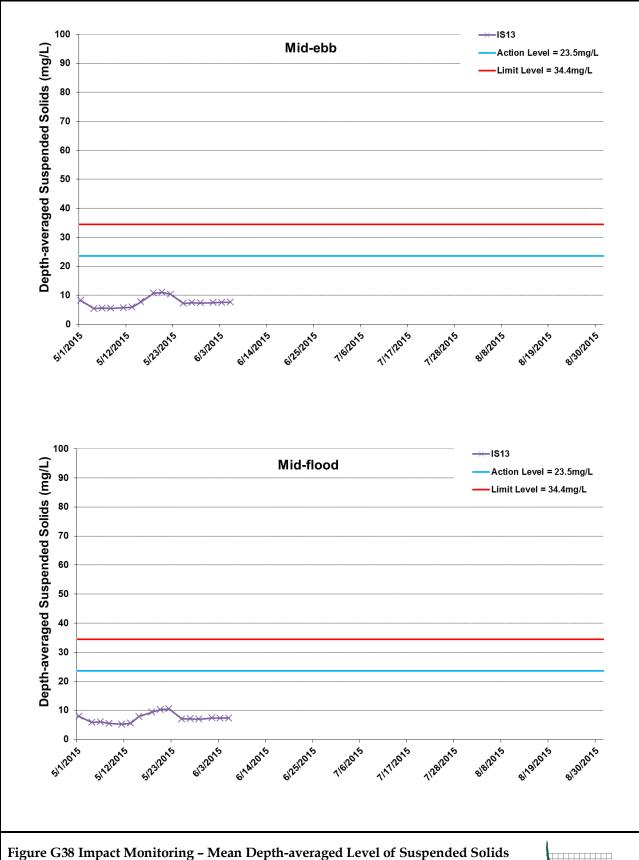


Figure G38 Impact Monitoring – Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at IS13. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



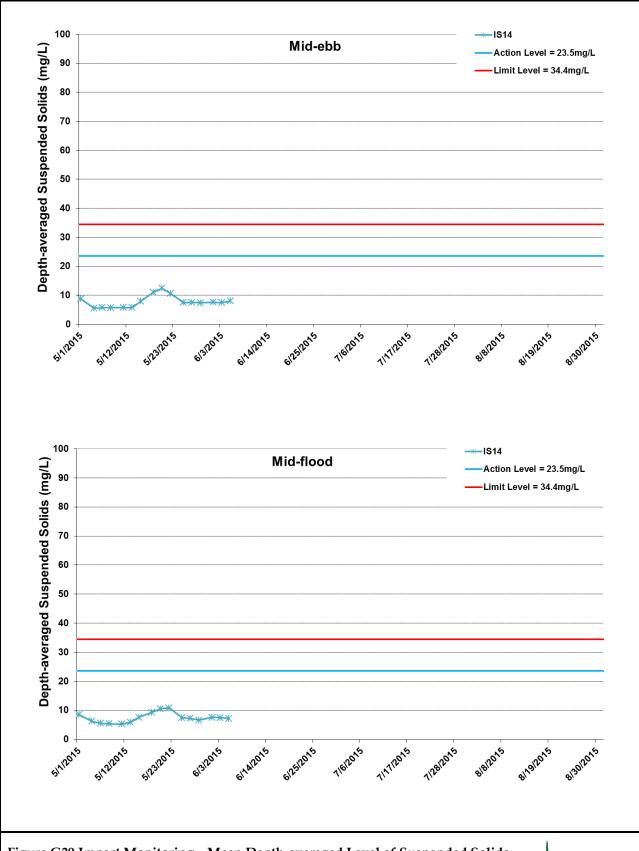


Figure G39 Impact Monitoring - Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at IS14. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



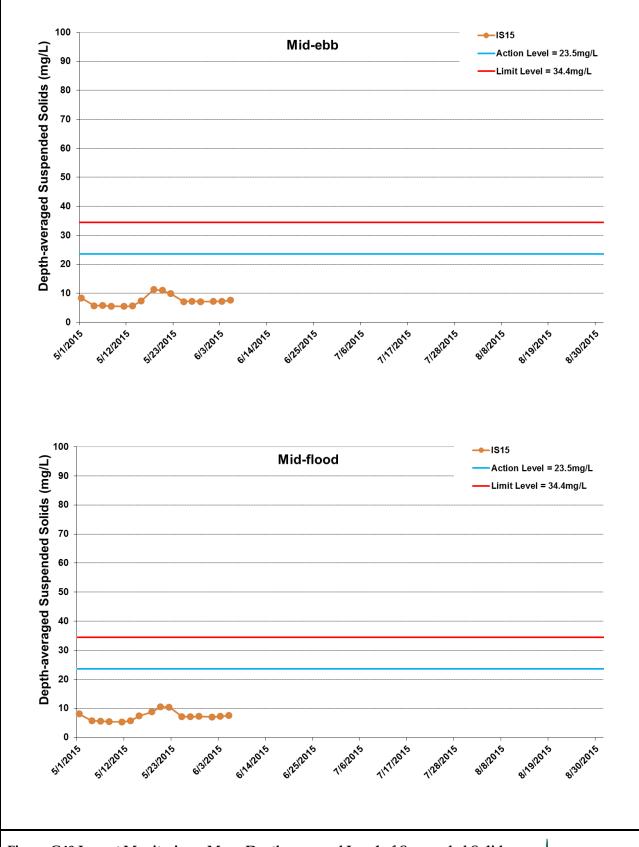


Figure G40 Impact Monitoring - Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at IS15. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



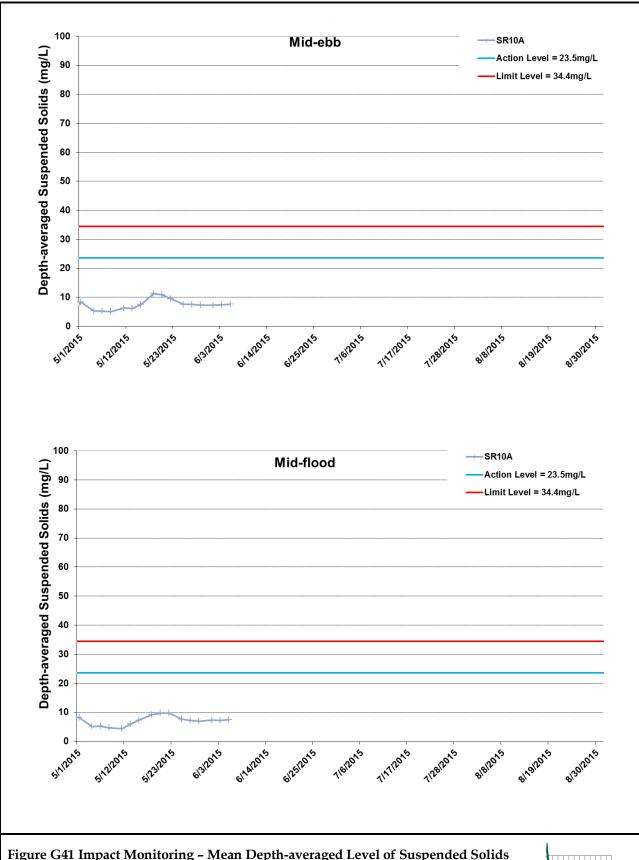


Figure G41 Impact Monitoring – Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at SR10A. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



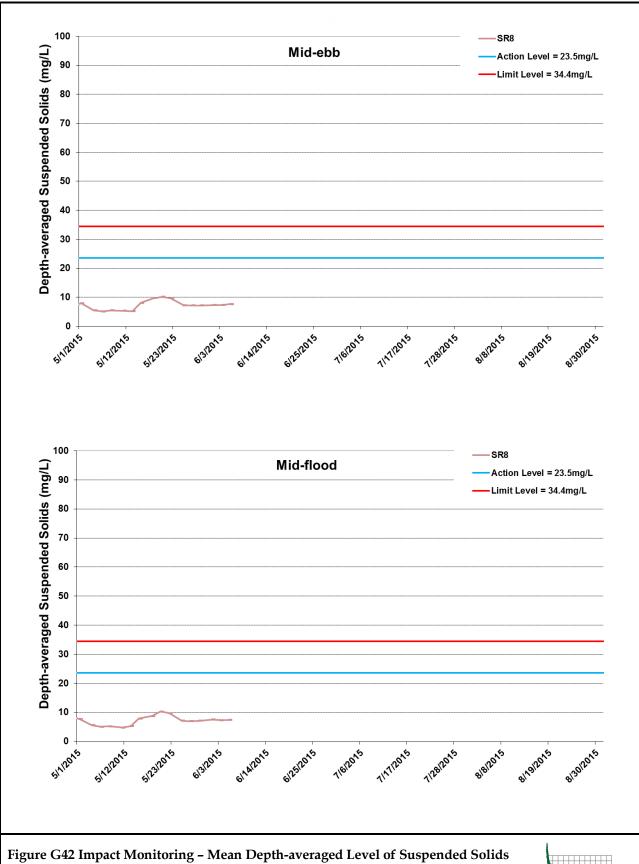


Figure G42 Impact Monitoring – Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at SR8. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



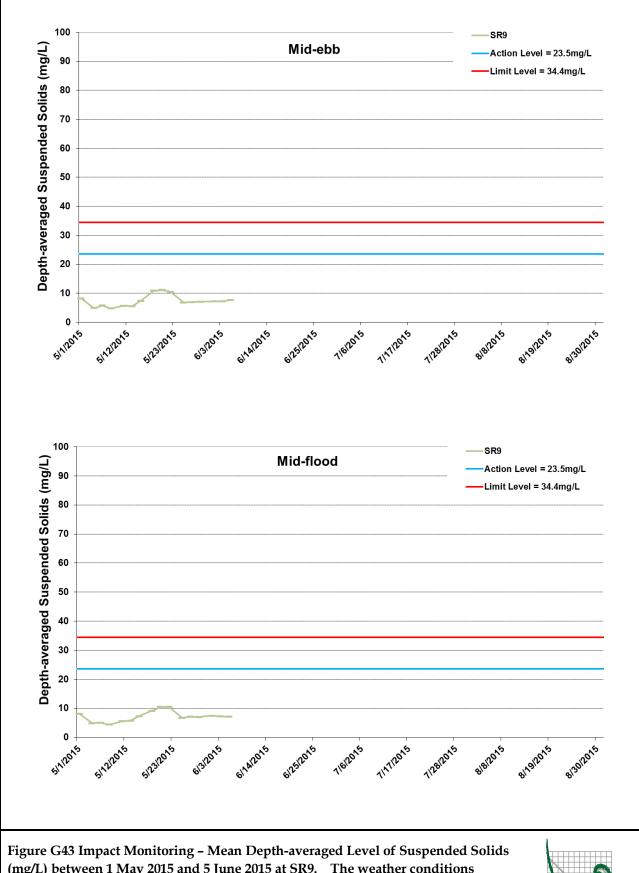


Figure G43 Impact Monitoring – Mean Depth-averaged Level of Suspended Solids (mg/L) between 1 May 2015 and 5 June 2015 at SR9. The weather conditions during the monitoring period varied mostly from sunny to cloudy. No marine works was undertaken during the reporting period.



Appendix H

Impact Dolphin Monitoring Survey

HK j efacean research project 香港鯨豚研究計劃

HK CETACEAN RESEARCH PROJECT

香港鯨豚研究計劃

CONTRACT NO. HY/2012/08

Hong Kong-Zhuhai-Macao Bridge Tuen Mun – Chek Lap Kok Link (Northern Connection Sub-sea Tunnel Section) Dolphin Quarterly Monitoring

7th Quarterly Progress Report (June-August 2015) submitted to Dragages – Bouygues Joint Venture & ERM Hong Kong Ltd.

Submitted by Samuel K.Y. Hung, Ph.D., Hong Kong Cetacean Research Project

23 September 2015

1. Introduction

- 1.1. As part of the Hong Kong-Zhuhai-Macao Bridge, the Tuen Mun-Chek Lap Kok Link (TM-CLKL) Northern Connection Sub-sea Tunnel Section (Contract no. HY/2012/08) comprises the sub-sea TBM tunnels (two tubes with cross passages) across the Urmston Road to connect Tuen Area 40 and Hong Kong Boundary Crossing Facilities (HKBCF) of approximately 4 km in length with dual 2-lane carriageway, the tunnels at both the southern landfall and the northern landfall for construction of approach roads to the sub-sea TBM tunnels of approximately 1.5 km in length, as well as the northern landfall reclamation of approximately 16.5 hectares and about 20.km long seawalls. Dragages Bouygues Joint Venture (hereinafter called the "Contractor") was awarded as the main contractor for the Northern Connection Sub-sea Tunnel Section, and ERM Hong Kong Limited would serve as the Environmental Team to implement the Environmental Monitoring and Audit (EM&A) programme.
- 1.2. According to the updated EM&A Manual (for TM-CLKL), monthly line-transect vessel surveys for Chinese White Dolphin should be conducted to cover the Northwest (NWL) and Northeast Lantau (NEL) survey areas as in AFCD annual marine mammal monitoring programme. However, as such surveys have been undertaken by the HKLR03 and HKBCF projects in the same areas (i.e. NWL and NEL), a combined monitoring approach is recommended by the Highways Department, that the TM-CLKL EM&A project can utilize the monitoring data collected by HKLR03 or HKBCF project to avoid any redundancy in monitoring effort. Such exemption for the dolphin monitoring will end upon the completion of the dolphin monitoring carried out by HKLR03 contract.
- 1.3. In November 2013, the Director of Hong Kong Cetacean Research Project (HKCRP), Dr. Samuel Hung, has been appointed by ERM Hong Kong Limited as the dolphin specialist for the TM-CLKL Northern Connection Sub-sea Tunnel Section EM&A project. He is responsible for the dolphin monitoring study, including the data collection on Chinese



HK CETACEAN RESEARCH PROJECT

香港鯨豚研究計劃

White Dolphins during the construction phase (i.e. impact period) of the TM-CLKL project in Northwest Lantau (NWL) and Northeast Lantau (NEL) survey areas.

- 1.4. During the construction period of HKLR, the dolphin specialist would be in charge of reviewing and collating information collected by HKLR03 dolphin monitoring programme to examine any potential impacts of TM-CLKL construction works on the dolphins.
- 1.5. From the monitoring results, any changes in dolphin occurrence within the study area will be examined for possible causes, and appropriate actions and additional mitigation measures will be recommended as necessary.
- 1.6. This report is the seventh quarterly progress report under the TM-CLKL construction phase dolphin monitoring programme submitted to the Contractor, summarizing the results of the surveys findings during the period of June to August 2015, utilizing the survey data collected by HKLR03 project.

2. Monitoring Methodology

- 2.1. Vessel-based Line-transect Survey
- 2.1.1. According to the requirement of the updated EM&A manual, dolphin monitoring programme should cover all transect lines in NEL and NWL survey areas (see Figure 1) twice per month throughout the entire construction period. The co-ordinates of all transect lines conducted during the HKLR03 dolphin monitoring surveys are shown in Table 1.

Table 1 Co-ordinates of transect lines conducted by HKLR03 project

Line No.		Easting	Northing	Line No.		Easting	Northing
1	Start Point	804671	814577	13	Start Point	816506	819480
1	End Point	804671	831404	13	End Point	816506	824859
2	Start Point	805475	815457	14	Start Point	817537	820220
2	End Point	805477	826654	14	End Point	817537	824613
3	Start Point	806464	819435	15	Start Point	818568	820735
3	End Point	806464	822911	15	End Point	818568	824433
4	Start Point	807518	819771	16	Start Point	819532	821420
4	End Point	807518	829230	16	End Point	819532	824209
5	Start Point	808504	820220	17	Start Point	820451	822125
5	End Point	808504	828602	17	End Point	820451	823671
6	Start Point	809490	820466	18	Start Point	821504	822371
6	End Point	809490	825352	18	End Point	821504	823761
7	Start Point	810499	820690	19	Start Point	822513	823268



HK CETACEAN RESEARCH PROJECT

香港鯨豚研究計劃

7	End Point	810499	824613	19	End Point	822513	824321
8	Start Point	811508	820847	20	Start Point	823477	823402
8	End Point	811508	824254	20	End Point	823477	824613
9	Start Point	812516	820892	21	Start Point	805476	827081
9	End Point	812516	824254	21	End Point	805476	830562
10	Start Point	813525	820872	22	Start Point	806464	824033
10	End Point	813525	824657	22	End Point	806464	829598
11	Start Point	814556	818449	23	Start Point	814559	821739
11	End Point	814556	820992	23	End Point	814559	824768
12	Start Point	815542	818807				
12	End Point	815542	824882				

- 2.1.2. The HKLR03 survey team used standard line-transect methods (Buckland et al. 2001) to conduct the systematic vessel surveys, and followed the same technique of data collection that has been adopted over the last 16 years of marine mammal monitoring surveys in Hong Kong developed by HKCRP (see Hung 2013, 2014). For each monitoring vessel survey, a 15-m inboard vessel with an open upper deck (about 4.5 m above water surface) was used to make observations from the flying bridge area.
- 2.1.3. Two experienced observers (a data recorder and a primary observer) made up the on-effort survey team, and the survey vessel transited different transect lines at a constant speed of 13-15 km per hour. The data recorder searched with unaided eyes and filled out the datasheets, while the primary observer searched for dolphins and porpoises continuously through 7 x 50 *Fujinon* marine binoculars. Both observers searched the sea ahead of the vessel, between 270° and 90° (in relation to the bow, which is defined as 0°). One to two additional experienced observers were available on the boat to work in shift (i.e. rotate every 30 minutes) in order to minimize fatigue of the survey team members. All observers were experienced in small cetacean survey techniques and identifying local cetacean species.
- 2.1.4. During on-effort survey periods, the survey team recorded effort data including time, positions (latitude and longitude), weather conditions (Beaufort sea state and visibility), and distance traveled in each series (a continuous period of search effort) with the assistance of a handheld GPS (*Garmin eTrex Legend*).
- 2.1.5. Data including time, position and vessel speed were also automatically and continuously logged by handheld GPS throughout the entire survey for subsequent review.
- 2.1.6. When dolphins were sighted, the survey team would end the survey effort, and immediately record the initial sighting distance and angle of the dolphin group from the survey vessel, as well as the sighting time and position. Then the research vessel was diverted from its course to approach the animals for species identification, group size estimation, assessment of group composition, and behavioural observations. The perpendicular distance (PSD) of the dolphin group to the transect line was later calculated



HK CETACEAN RESEARCH PROJECT 香港鯨豚研究計劃

from the initial sighting distance and angle.

2.1.7. Survey effort being conducted along the parallel transect lines that were perpendicular to the coastlines (as indicated in Figure 1) was labeled as "primary" survey effort, while the survey effort conducted along the connecting lines between parallel lines was labeled as "secondary" survey effort. According to HKCRP long-term dolphin monitoring data, encounter rates of Chinese white dolphins deduced from effort and sighting data collected along primary and secondary lines were similar in NEL and NWL survey areas. Therefore, both primary and secondary survey effort were presented as on-effort survey effort in this report.

2.2. Photo-identification Work

- 2.2.1. When a group of Chinese White Dolphins were sighted during the line-transect survey, the HKLR03 survey team would end effort and approach the group slowly from the side and behind to take photographs of them. Every attempt was made to photograph every dolphin in the group, and even photograph both sides of the dolphins, since the colouration and markings on both sides may not be symmetrical.
- 2.2.2. A professional digital camera (*Canon* EOS 7D or 60D model), equipped with long telephoto lenses (100-400 mm zoom), were available on board for researchers to take sharp, close-up photographs of dolphins as they surfaced. The images were shot at the highest available resolution and stored on Compact Flash memory cards for downloading onto a computer.
- 2.2.3. All digital images taken in the field were first examined, and those containing potentially identifiable individuals were sorted out. These photographs would then be examined in greater detail, and were carefully compared to the existing Chinese White Dolphin photo-identification catalogue maintained by HKCRP since 1995.
- 2.2.4. Chinese White Dolphins can be identified by their natural markings, such as nicks, cuts, scars and deformities on their dorsal fin and body, and their unique spotting patterns were also used as secondary identifying features (Jefferson 2000).
- 2.2.5. All photographs of each individual were then compiled and arranged in chronological order, with data including the date and location first identified (initial sighting), re-sightings, associated dolphins, distinctive features, and age classes entered into a computer database.

2.3. Data Analysis

2.3.1. Distribution Analysis – The line-transect survey data was integrated with the Geographic Information System (GIS) in order to visualize and interpret different spatial and temporal patterns of dolphin distribution using sighting positions. Location data of dolphin groups were plotted on map layers of Hong Kong using a desktop GIS (ArcView[©] 3.1) to examine their distribution patterns in details. The dataset was also stratified into



HK CETACEAN RESEARCH PROJECT 香港鯨豚研究計劃

different subsets to examine distribution patterns of dolphin groups with different categories of group sizes, young calves and activities.

2.3.2. Encounter rate analysis – Encounter rates of Chinese white dolphins (number of on-effort sightings per 100 km of survey effort, and total number of dolphins sighted on-effort per 100 km of survey effort) were calculated in NEL and NWL survey areas in relation to the amount of survey effort conducted during each month of monitoring survey. Only data collect under Beaufort 3 or below condition would be used for the encounter rate analyses. Dolphin encounter rates were calculated in two ways for comparisons with the HZMB baseline monitoring results as well as to AFCD long-term marine mammal monitoring results.

Firstly, for the comparison with the HZMB baseline monitoring results, the encounter rates were calculated using primary survey effort alone. The average encounter rate of sightings (STG) and average encounter rate of dolphins (ANI) were deduced based on the encounter rates from six events during the present quarter (i.e. six sets of line-transect surveys in North Lantau), which was also compared with the one deduced from the six events during the baseline period (i.e. six sets of line-transect surveys in North Lantau).

Secondly, the encounter rates were calculated using both primary and secondary survey effort collected under Beaufort 3 or below condition as in AFCD long-term monitoring study. The encounter rate of sightings and dolphins were deduced by dividing the total number of on-effort sightings (STG) and total number of dolphins (ANI) by the amount of survey effort for the present quarterly period.

2.3.3. Quantitative grid analysis on habitat use – To conduct quantitative grid analysis of habitat use, positions of on-effort sightings of Chinese White Dolphins collected during the quarterly impact phase monitoring period were plotted onto 1-km² grids among NWL and NEL survey areas on GIS. Sighting densities (number of on-effort sightings per km²) and dolphin densities (total number of dolphins from on-effort sightings per km²) were then calculated for each 1 km by 1 km grid with the aid of GIS. Sighting density grids and dolphin density grids were then further normalized with the amount of survey effort conducted within each grid. The total amount of survey effort spent on each grid was calculated by examining the survey coverage on each line-transect survey to determine how many times the grid was surveyed during the study period. For example, when the survey boat traversed through a specific grid 50 times, 50 units of survey effort were counted for that grid. With the amount of survey effort calculated for each grid, the sighting density and dolphin density of each grid were then normalized (i.e. divided by the unit of survey effort).

The newly-derived unit for sighting density was termed SPSE, representing the number of on-effort sightings per 100 units of survey effort. In addition, the derived unit for actual dolphin density was termed DPSE, representing the number of dolphins per 100 units of survey effort. Among the 1-km² grids that were partially covered by land, the percentage of sea area was calculated using GIS tools, and their SPSE and DPSE values were adjusted accordingly. The following formulae were used to estimate SPSE and DPSE in each 1-km² grid within the study area:



HK CETACEAN RESEARCH PROJECT 香港鯨豚研究計劃

SPSE = ((S / E) x 100) / SA% DPSE = ((D / E) x 100) / SA%

where S = total number of on-effort sightings

D = total number of dolphins from on-effort sightings

E = total number of units of survey effort

SA% = percentage of sea area

2.3.4. Behavioural analysis – When dolphins were sighted during vessel surveys, their behaviour was observed. Different activities were categorized (i.e. feeding, socializing, traveling, and milling/resting) and recorded on sighting datasheets. This data was then input into a separate database with sighting information, which can be used to determine the distribution of behavioural data with a desktop GIS. Distribution of sightings of dolphins engaged in different activities and behaviours would then be plotted on GIS and carefully examined to identify important areas for different activities of the dolphins.

2.3.5. Ranging pattern analysis – Location data of individual dolphins that occurred during the 3-month impact phase monitoring period were obtained from the dolphin sighting database and photo-identification catalogue. To deduce home ranges for individual dolphins using the fixed kernel methods, the program Animal Movement Analyst Extension, was loaded as an extension with ArcView 3.1 along with another extension Spatial Analyst 2.0. Using the fixed kernel method, the program calculated kernel density estimates based on all sighting positions, and provided an active interface to display kernel density plots. The kernel estimator then calculated and displayed the overall ranging area at 95% UD level.

3. Monitoring Results

- 3.1. Summary of survey effort and dolphin sightings
- 3.1.1. During the period of June to August 2015, six sets of systematic line-transect vessel surveys were conducted under the HKLR03 monitoring works to cover all transect lines in NWL and NEL survey areas twice per month.
- 3.1.2. From these HKLR03 surveys, a total of 900.64 km of survey effort was collected, with 92.8% of the total survey effort being conducted under favourable weather conditions (i.e. Beaufort Sea State 3 or below with good visibility). Among the two areas, 345.58 km and 555.06 km of survey effort were conducted in NEL and NWL survey areas respectively.
- 3.1.3. The total survey effort conducted on primary lines was 655.74 km, while the effort on secondary lines was 244.90 km. Survey effort conducted on both primary and secondary lines were considered as on-effort survey data. A summary table of the survey effort is shown in Appendix I.



HK CETACEAN RESEARCH PROJECT

香港鯨豚研究計劃

- 3.1.4. During the six sets of HKLR03 monitoring surveys in June to August 2015, a total of 12 groups of 42 Chinese White Dolphins were sighted. All dolphin sightings were made during on-effort search, and all of them were made on primary lines. In this quarterly period, all except one dolphin groups were sighted in NWL, while only one group of a lone animal was sighted in NEL. Notably, this was the first dolphin sighted in NEL since July 2014 during HKLR03 monitoring surveys. A summary table of the dolphin sightings is shown in Appendix II.
- 3.2. Distribution
- 3.2.1. Distribution of dolphin sightings made during monitoring surveys in June to August 2015 is shown in Figure 1. Dolphin sightings made in the present quarter were only clustered to the north and northeast of Lung Kwu Chau, and to the southwestern end of NWL survey area near the HKLR09 alignment (Figure 1). The lone dolphin sighted in NEL was located between Shum Shui Kok and Yam O, while there was another group of two dolphins sighted to the west of Sha Chau during this quarter (Figure 1).
- 3.2.2. Notably, none of the dolphin groups were sighted in the vicinity of TMCLKL northern landfall or southern viaduct section, and the HKLR03/HKBCF reclamation site (Figure 1). On the other hand, three sightings (with two lone individuals in two sightings and another group of four dolphins) were made in the vicinity of the HKLR09 alignment (Figure 1).
- 3.2.3. Sighting distribution of the present impact phase monitoring period (June to August 2015) was compared to the one during the baseline monitoring period (September to November 2011). In the present quarter, dolphins have almost vacated the NEL region, which was in stark contrast to their frequent occurrence around the Brothers Islands, near Shum Shui Kok and in the vicinity of HKBCF reclamation site during the baseline period (Figure 1). The nearly complete abandonment of NEL region by the dolphins has been consistently recorded in the past ten quarters of HKLR03 monitoring, which has resulted in extremely low to zero dolphin encounter rate in this area.
- 3.2.4. In NWL survey area, dolphin occurrence was also drastically different between the baseline and impact phase periods. During the present impact monitoring period, much fewer dolphins occurred in this survey area than during the baseline period, when many of the dolphin sightings were concentrated between Lung Kwu Chau and Black Point, around Sha Chau, near Pillar Point and to the west of the Chek Lap Kok Airport (Figure 1).
- 3.2.5. Another comparison in dolphin distribution was made between the three quarterly periods of summer months in 2013, 2014 and 2015 (Figure 2). Among the three summer periods, only one dolphin sighting was made in NEL in both 2014 and 2015, while there were a number of sightings made there in 2013 (Figure 2).
- 3.2.6. Dramatic changes in dolphin distribution in NWL waters were also observed in the summer months during the three-year period (Figure 2). In 2013, dolphin regularly occurred throughout the NWL survey area, with higher concentrations of sightings around Sha Chau, Lung Kwu Chau, near Black Point and Pillar Point, and to the north of airport platform. In 2014, dolphin still occurred around Sha Chau and Lung Kwu Chau at a



香港鯨豚研究計劃

high level, but less frequently in the middle portion of North Lantau region. In 2015, they infrequently occurred in NWL survey area with the only concentration around Lung Kwu Chau while they generally absent throughout this area. The temporal trend indicated that dolphin usage in the NWL region has progressively diminished during the summer months in the past few years.

3.3. Encounter rate

3.3.1. During the present quarterly period, the encounter rates of Chinese White Dolphins deduced from the survey effort and on-effort sighting data from the primary transect lines under favourable conditions (Beaufort 3 or below) for each set of the HKLR03 surveys in NEL and NWL are shown in Table 2. The average encounter rates deduced from the six sets of HKLR03 surveys were also compared with the ones deduced from the baseline monitoring period (September – November 2011) (Table 3).

Table 2. Dolphin encounter rates (sightings per 100 km of survey effort) during June-August 2015

SURVEY AREA	DOLPHIN MONITORING DATES	Encounter rate (STG) (no. of on-effort dolphin sightings per 100 km of survey effort)	Encounter rate (ANI) (no. of dolphins from all on-effort sightings per 100 km of survey effort)	
		Primary Lines Only	Primary Lines Only	
	Set 1 (2 & 10 Jun 2015)	0.00	0.00	
	Set 2 (24 & 26 Jun 2015)	2.64	2.64	
Northeast	Set 3 (2 & 7 Jul 2015)	0.00	0.00	
Lantau	Set 4 (22 & 27 Jul 2015)	0.00	0.00	
	Set 5 (10 & 14 Aug 2015)	0.00	0.00	
	Set 6 (19 & 28 Aug 2015)	0.00	0.00	
	Set 1 (2 & 10 Jun 2015)	1.51	15.15	
	Set 2 (24 & 26 Jun 2015)	0.00	0.00	
Northwest	Set 3 (2 & 7 Jul 2015)	1.69	3.38	
Lantau	Set 4 (22 & 27 Jul 2015)	3.46	6.92	
	Set 5 (10 & 14 Aug 2015)	0.00	0.00	
=	Set 6 (19 & 28 Aug 2015)	8.53	29.84	

- 3.3.2. To facilitate the comparison with the AFCD long-term monitoring results, the encounter rates were also calculated for the present quarter using both primary and secondary survey effort. The encounter rates of sightings (STG) and dolphins (ANI) in NWL were 2.04 sightings and 7.55 dolphins per 100 km of survey effort respectively, while the encounter rates of sightings (STG) and dolphins (ANI) in NEL were both 0.29 for this quarter.
- 3.3.3. In NEL, the average dolphin encounter rates (both STG and ANI) in the present three-month impact monitoring period were close to nil, and such low occurrence of dolphins in NEL have been consistently recorded in the past ten quarters of HKLR03 monitoring (Table 4). This is a serious concern that dolphin occurrence in NEL in the



香港鯨豚研究計劃

last ten quarters (0.0-1.0 for ER(STG) and 0.0-3.9 for ER(ANI)) have been exceptionally low when compared to the baseline period (Table 4). Dolphins have almost vacated from NEL waters since January 2014, with only two groups of five dolphins sighted since then despite consistent and intensive survey effort being conducted in this area.

Table 3. Comparison of average dolphin encounter rates from impact monitoring period (June-August 2015) and baseline monitoring period (September – November 2011) (Note: encounter rates deduced from the baseline monitoring period have been recalculated based only on survey effort and on-effort sighting data made along the primary transect lines under favourable conditions; ± denotes the standard deviation of the average encounter rates)

	Encounter	rate (STG)	Encounter rate (ANI)			
	(no. of on-effort dolph	in sightings per 100	(no. of dolphins from all on-effort sightings			
	km of surv	ey effort)	per 100 km c	of survey effort)		
	June - August 2015	September - November 2011	June - August 2015	September - November 2011		
Northeast Lantau	0.44 ± 1.08	6.00 ± 5.05	0.44 ± 1.08	22.19 ± 26.81		
Northwest Lantau	2.53 ± 3.20	9.85 ± 5.85	9.21 ± 11.57	44.66 ± 29.85		

Table 4. Comparison of average dolphin encounter rates in Northeast Lantau survey area from all quarters of impact monitoring period and baseline monitoring period (September-November 2011) (Note: encounter rates deduced from the baseline monitoring period have been recalculated based only on survey effort and on-effort sighting data made along the primary transect lines under favourable conditions; the encounter rates in summer months were highlighted in blue; ± denotes the standard deviation of the average encounter rates)

	Encounter rate (STG) (no. of on-effort dolphin sightings per 100 km of survey effort)	Encounter rate (ANI) (no. of dolphins from all on-effort sightings per 100 km of survey effort)
September-November 2011 (Baseline)	6.00 ± 5.05	22.19 ± 26.81
December 2012-February 2013 (Impact)	3.14 ± 3.21	6.33 ± 8.64
March-May 2013 (Impact)	0.42 ± 1.03	0.42 ± 1.03
June-August 2013 (Impact)	0.88 ± 1.36	3.91 ± 8.36
September-November 2013 (Impact)	1.01 ± 1.59	3.77 ± 6.49
December 2013-February 2014 (Impact)	0.45 ± 1.10	1.34 ± 3.29
March-May 2014 (Impact)	0.00	0.00
June-August 2014 (Impact)	0.42 ± 1.04	1.69 ± 4.15
September-November 2014 (Impact)	0.00	0.00
December 2014-February 2015 (Impact)	0.00	0.00
March-May 2015 (Impact)	0.00	0.00
June-August 2015 (Impact)	0.44 ± 1.08	0.44 ± 1.08



香港鯨豚研究計劃

- 3.3.4. Moreover, the average dolphin encounter rates (STG and ANI) in NWL during the present impact phase monitoring period were also much lower (reductions of 74.3% and 79.3% respectively) than the ones recorded in the 3-month baseline period, indicating a dramatic decline in dolphin usage of this survey area as well during the present impact phase period (Table 5).
- 3.3.5. Even for the same summer quarters, the dolphin encounter rates in NWL during summer 2015 were much lower than the ones recorded in summer 2013 and 2014 (Table 5).

Table 5. Comparison of average dolphin encounter rates in Northwest Lantau survey area from all quarters of impact monitoring period and baseline monitoring period (September-November 2011) (Note: encounter rates deduced from the baseline monitoring period have been recalculated based only on survey effort and on-effort sighting data made along the primary transect lines under favourable conditions; the encounter rates in summer months were highlighted in blue; ± denotes the standard deviation of the average encounter rates)

	Encounter rate (STG)	Encounter rate (ANI)
	(no. of on-effort dolphin	(no. of dolphins from all
	sightings per 100 km of	on-effort sightings per 100
	survey effort)	km of survey effort)
September-November 2011 (Baseline)	9.85 ± 5.85	44.66 ± 29.85
December 2012-February 2013 (Impact)	8.36 ± 5.03	35.90 ± 23.10
March-May 2013 (Impact)	7.75 ± 3.96	24.23 ± 18.05
June-August 2013 (Impact)	6.56 ± 3.68	27.00 ± 18.71
September-November 2013 (Impact)	8.04 ± 1.10	32.48 ± 26.51
December 2013-February 2014 (Impact)	8.21 ± 2.21	32.58 ± 11.21
March-May 2014 (Impact)	6.51 ± 3.34	19.14 ± 7.19
June-August 2014 (Impact)	4.74 ± 3.84	17.52 ± 15.12
September-November 2014 (Impact)	5.10 ± 4.40	20.52 ± 15.10
December 2014-February 2015 (Impact)	2.91 ± 2.69	11.27 ± 15.19
March-May 2015 (Impact)	0.47 ± 0.73	2.36 ± 4.07
June-August 2015 (Impact)	2.53 ± 3.20	9.21 ± 11.57

- 3.3.6. Notably, for the TMCLKL dolphin monitoring programme, the past three quarters have all triggered the Limit Levels under the Event and Action Plan.
- 3.3.7. As discussed recently in Hung (2015), the dramatic decline in dolphin usage of NEL waters in the past few years (including the declines in abundance, encounter rate and habitat use in NEL, as well as shifts of individual core areas and ranges away from NEL waters) was possibly related to the HZMB construction works that were commenced since 2012. It appeared that such noticeable decline has already extended to NWL waters progressively in 2013-2015.
- 3.3.8. A two-way ANOVA with repeated measures and unequal sample size was conducted to



HK CETACEAN RESEARCH PROJECT 香港鯨豚研究計劃

examine whether there were any significant differences in the average encounter rates between the baseline and impact monitoring periods. The two variables that were examined included the two periods (baseline and impact phases) and two locations (NEL and NWL).

- 3.3.9. For the comparison between the baseline period and the present quarter (eleventh quarter of the HKLR03 impact phase monitoring being assessed), the p-values for the differences in average dolphin encounter rates of STG and ANI were 0.0064 and 0.0270 respectively. If the alpha value is set at 0.05, significant differences were detected between the baseline and present quarters in both dolphin encounter rates of STG and ANI.
- 3.3.10. For the comparison between the baseline period and the cumulative quarters in impact phase (i.e. first eleven quarters of the HKLR03 impact phase monitoring being assessed), the p-values for the differences in average dolphin encounter rates of STG and ANI were 0.00020 and 0.00005 respectively. Even if the alpha value is set at 0.01, significant differences were detected in both the average dolphin encounter rates of STG and ANI (i.e. between the two periods and the locations).
- 3.3.11. As indicated in both dolphin distribution patterns and encounter rates, dolphin usage has been significantly reduced in both NEL and NWL survey areas during the present quarterly period, and such low occurrence of dolphins has also been consistently documented in previous quarters. This raises serious concern, as the timing of the decline in dolphin usage in North Lantau waters coincided well with the HZMB-related construction activities (Hung 2015).
- 3.3.12. To ensure the continuous usage of North Lantau waters by the dolphins, every possible measure should be implemented by the contractors and relevant authorities of HZMB-related works to minimize all disturbances to the dolphins.
- 3.4. Group size
- 3.4.1. Group size of Chinese White Dolphins ranged from one to ten individuals per group in North Lantau region during June to August 2015. The average dolphin group sizes from these three months were compared with the ones deduced from the baseline period in September to November 2011, as shown in Table 6.
- 3.4.2. The average dolphin group sizes in NWL waters during June to August 2015 were slightly smaller than the ones recorded during the three-month baseline period (Table 6). Half of the 12 groups were composed of 1-3 individuals only, while five other groups were moderate in size with 4-5 individuals per group. On the other hand, only one large group of 10 dolphins was sighted during the present quarterly period.



香港鯨豚研究計劃

Table 6. Comparison of average dolphin group sizes from impact monitoring period (June – August 2015) and baseline monitoring period (September – November 2011) (Note: ± denotes the standard deviation of the average group size)

	Average Dolph	Average Dolphin Group Size								
	June – August 2015 September – November 202									
Overall	3.50 ± 2.65 (n = 12)	3.72 ± 3.13 (n = 66)								
Northeast Lantau	1.00 (n = 1)	3.18 ± 2.16 (n = 17)								
Northwest Lantau	3.73 ± 2.65 (n = 11)	3.92 ± 3.40 (n = 49)								

- 3.4.3. None of the larger dolphin groups were sighted near the TMCLKL alignment during the present monitoring period (Figure 3).
- 3.5. Habitat use
- 3.5.1. From June to August 2015, the only area being heavily utilized by Chinese White Dolphins was around Lung Kwu Chau in North Lantau waters (Figures 4a and 4b). Only one grid in NEL recorded the presence of dolphin in the present quarter with low DPSE value (Figure 4b). Moreover, all grids near the TMCLKL alignment and HKLR03/HKBCF reclamation sites did not record any presence of dolphins during on-effort search in the present quarterly period, but a few grids in the vicinity of HKLR09 alignment recorded moderate dolphin densities (Figure 4b).
- 3.5.2. It should be emphasized that the amount of survey effort collected in each grid during the three-month period was fairly low (6-12 units of survey effort for most grids), and therefore the habitat use pattern derived from the three-month dataset should be treated with caution. A more complete picture of dolphin habitat use pattern should be examined when more survey effort for each grid will be collected throughout the impact phase monitoring programme.
- 3.5.3. When compared with the habitat use patterns during the baseline period, dolphin usage in NEL and NWL has dramatically diminished in both areas during the present impact monitoring period (Figure 5). During the baseline period, many grids between Siu Mo To and Shum Shui Kok recorded moderately high to high dolphin densities, which was in stark contrast to rare occurrence of dolphins during the present impact phase period (Figure 5).
- 3.5.4. The density patterns were also very different in NWL between the baseline and impact phase monitoring periods, with higher dolphin usage around Sha Chau, near Black Point, to the west of the airport, as well as between Pillar Point and airport platform during the baseline period. In contrast, only the Lung Kwu Chau area recorded high densities of dolphins during the present impact phase period (Figure 5).



香港鯨豚研究計劃

- 3.6. Mother-calf pairs
- 3.6.1. During the present quarterly period, no young calves (i.e. unspotted calves or unspotted juveniles) for the third consecutive quarter among the seven quarters of TMCLKL impact phase monitoring.
- 3.6.2. This absence of young calves is also in stark contrast to their regular occurrence during the baseline period. Their absences should be of a serious concern, and the occurrence of calves should be closely monitored in the upcoming quarters.
- 3.7. Activities and associations with fishing boats
- 3.7.1. Only one dolphin group was associated with feeding activity, while none of the 12 dolphin groups was associated with socializing, traveling or milling/resting activity during the three-month study period.
- 3.7.2. The percentage of sightings associated with feeding activities during the present impact phase period (8.3%) was similar to the one recorded during the baseline period (11.6%). However, the sample sizes on total numbers of dolphin sightings were very different between the two periods.
- 3.7.3. Distribution of dolphins engaged in various activities during the present three-month period and baseline period is shown in Figure 6. The only sighting engaged in feeding activity was located near Lung Kwu Chau (Figure 6). When compared to the baseline period, distribution of dolphin activities in the present quarter was drastically different during the present impact phase monitoring quarter (Figure 6).
- 3.7.4. As consistently recorded in the past monitoring quarters, none of the twelve dolphin groups was found to be associated with operating fishing vessels in North Lantau waters during the present impact phase period.
- 3.8. Summary of photo-identification works
- 3.8.1. From June to August 2015, over 1,500 digital photographs of Chinese White Dolphins were taken during the impact phase monitoring surveys for the photo-identification work.
- 3.8.2. In total, 21 individuals sighted 30 times altogether were identified (see summary table in Appendix III and photographs of identified individuals in Appendix IV). All of these re-sightings were made in NWL. The lone dolphin sighted in NEL during this quarter was too elusive to be photographed for identification.
- 3.8.3. The majority of identified individuals were sighted only once during the three-month period, with the exception of three individuals (CH34, NL136 and NL310) being twice and another three individuals (NL104, NL202 and NL286) being sighted thrice.
- 3.8.4. Notably, four of these 21 individuals (NL136, NL293, WL05 and WL124) were also sighted in West Lantau waters during the HKLR09 monitoring surveys during June to August 2015, implying that they have moved across the HKLR09 bridge alignment during the same three-month period.



HK CETACEAN RESEARCH PROJECT 香港鯨豚研究計劃

- 3.9. Individual range use
- 3.9.1. Ranging patterns of the 21 individuals identified during the three-month study period were determined by fixed kernel method, and are shown in Appendix V.
- 3.9.2. All identified dolphins sighted in the present quarter were utilizing NWL waters only, but have avoided the NEL waters where many of them have utilized as their core areas in the past (Appendix V). Moreover, this is in contrary to the extensive movements between NEL and NWL survey areas observed in the earlier impact monitoring quarters as well as during the baseline period.
- 3.9.3. Notably, one individual (NL136) consistently sighted in NWL and NEL waters in the past have extended its range use to WL waters in the present quarter. In the upcoming quarter, individual range use and movements should be continuously monitored to examine whether there has been any consistent shifts of individual home ranges from North Lantau to West or Southwest Lantau, as such shift could possibly be related to the HZMB-related construction works (see Hung 2015).

4. Conclusion

- 4.1. During this quarter of dolphin monitoring, no adverse impact from the activities of the TMCLKL construction project on Chinese White Dolphins was noticeable from general observations.
- 4.2. Although the dolphins infrequently occurred along the alignment of TMCLKL northern connection sub-sea tunnel section in the past and during the baseline monitoring period, it is apparent that dolphin usage has been significantly reduced in NEL, and many individuals have shifted away from the important habitat around the Brothers Islands.
- 4.3. It is critical to monitor the dolphin usage in North Lantau region in the upcoming quarters, to determine whether the dolphins are continuously affected by the various construction activities in relation to the HZMB-related works, and whether suitable mitigation measure can be applied to revert the situation.


5. References

- Buckland, S. T., Anderson, D. R., Burnham, K. P., Laake, J. L., Borchers, D. L., and Thomas, L. 2001. Introduction to distance sampling: estimating abundance of biological populations. Oxford University Press, London.
- Hung, S. K. 2013. Monitoring of Marine Mammals in Hong Kong waters: final report (2012-13). An unpublished report submitted to the Agriculture, Fisheries and Conservation Department, 168 pp.



香港鯨豚研究計劃

- Hung, S. K. 2014. Monitoring of marine mammals in Hong Kong waters data collection: final report (2013-14). An unpublished report submitted to the Agriculture, Fisheries and Conservation Department of Hong Kong SAR Government, 231 pp.
- Hung, S. K. 2015. Monitoring of marine mammals in Hong Kong waters data collection: final report (2014-15). An unpublished report submitted to the Agriculture, Fisheries and Conservation Department of Hong Kong SAR Government, 198 pp.
- Jefferson, T. A. 2000. Population biology of the Indo-Pacific hump-backed dolphin in Hong Kong waters. Wildlife Monographs 144:1-65.

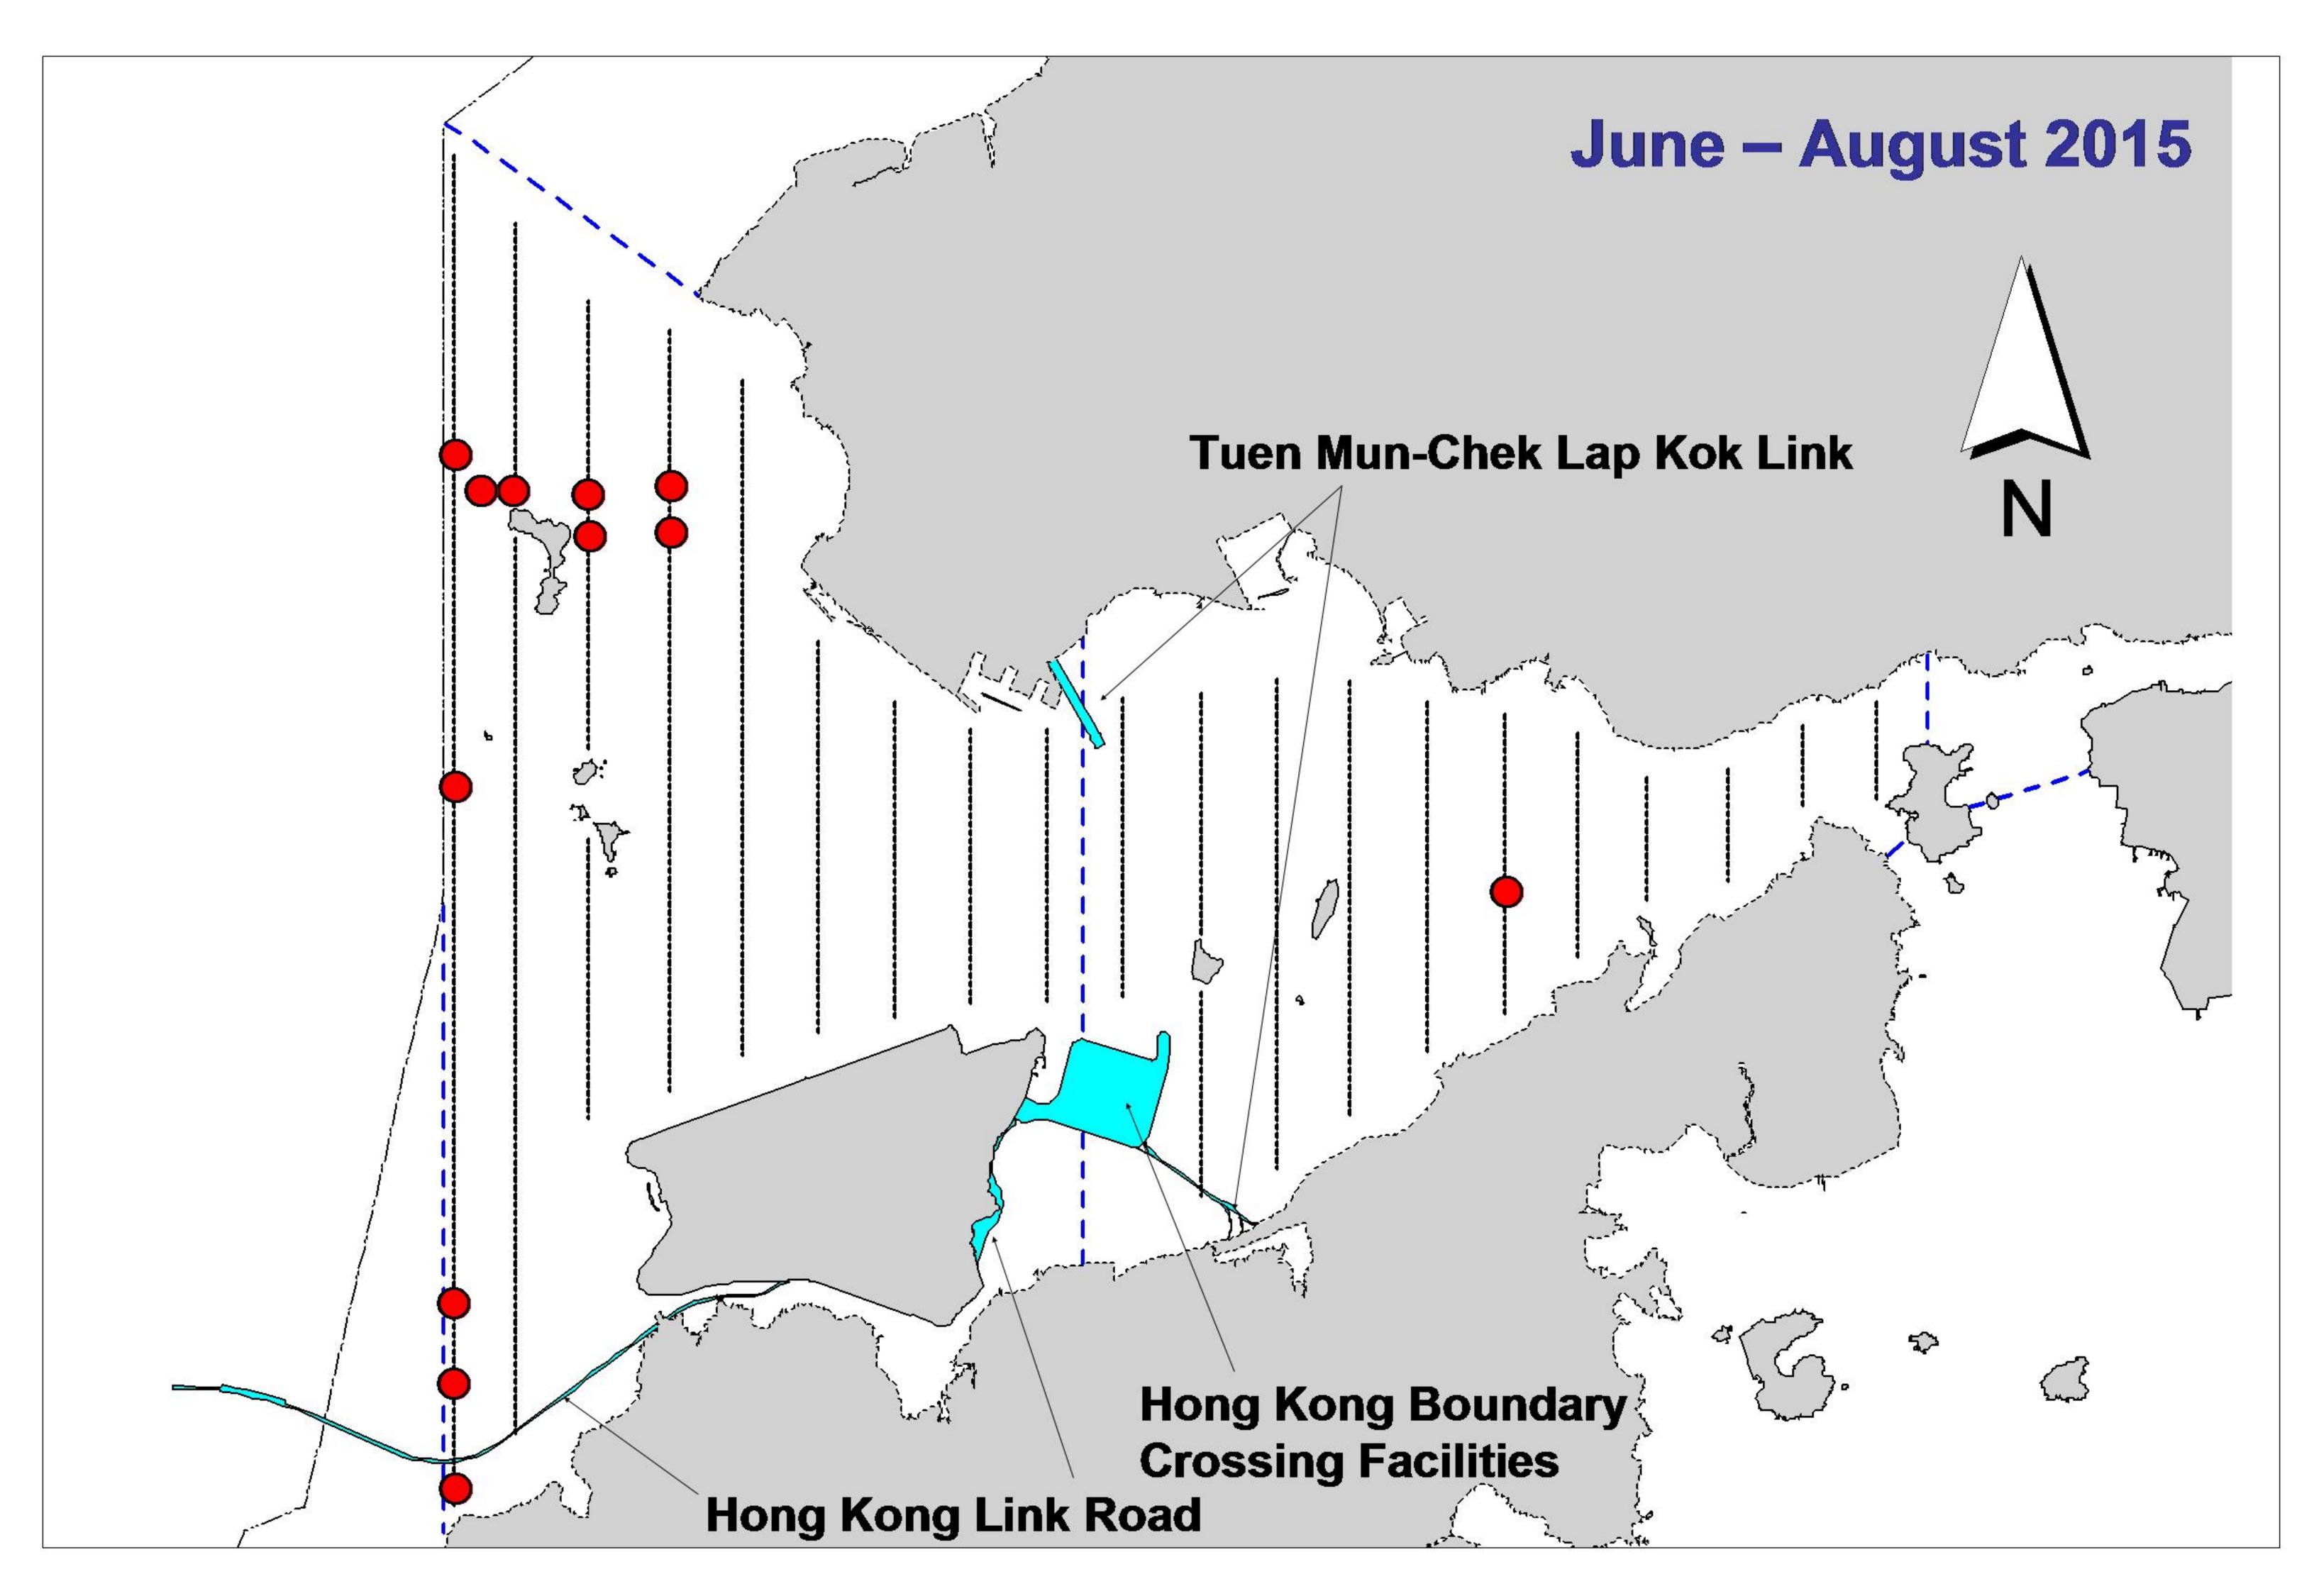

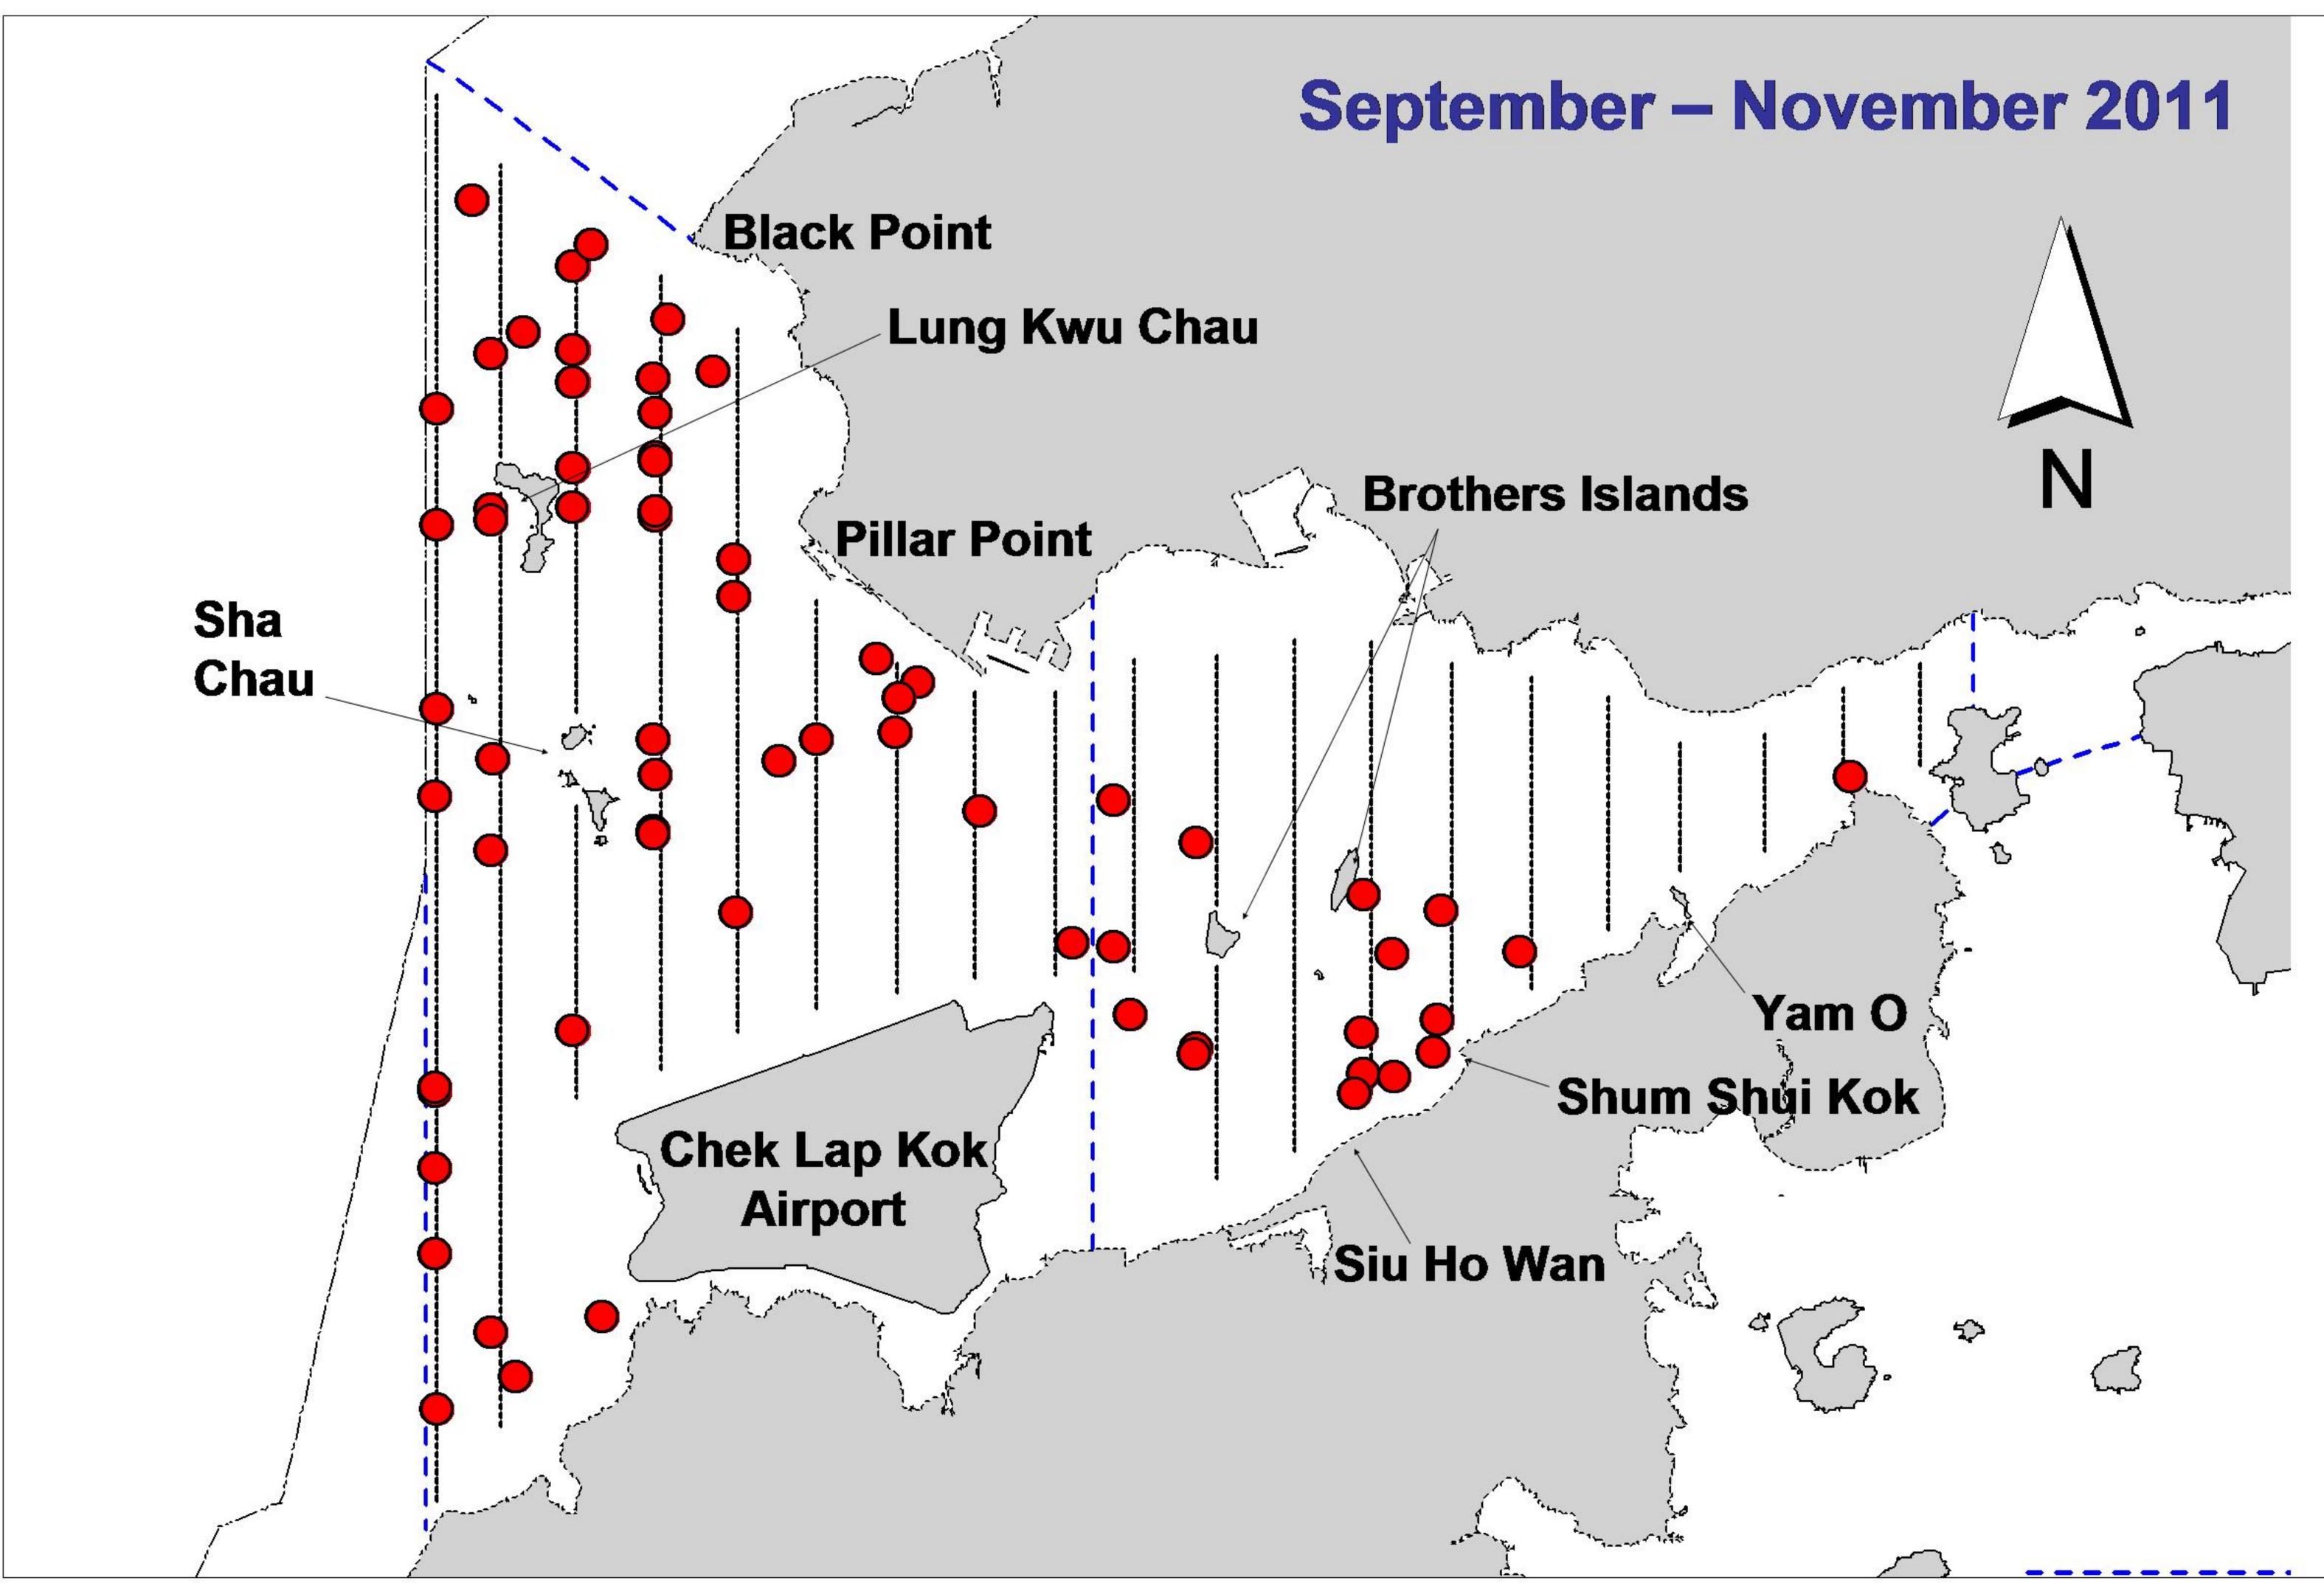


Figure 1. Distribution of Chinese white dolphin sighting in Northwest and Northeast Lantau during HKLR03 impact phase (top) and baseline monitoring surveys (bottom)

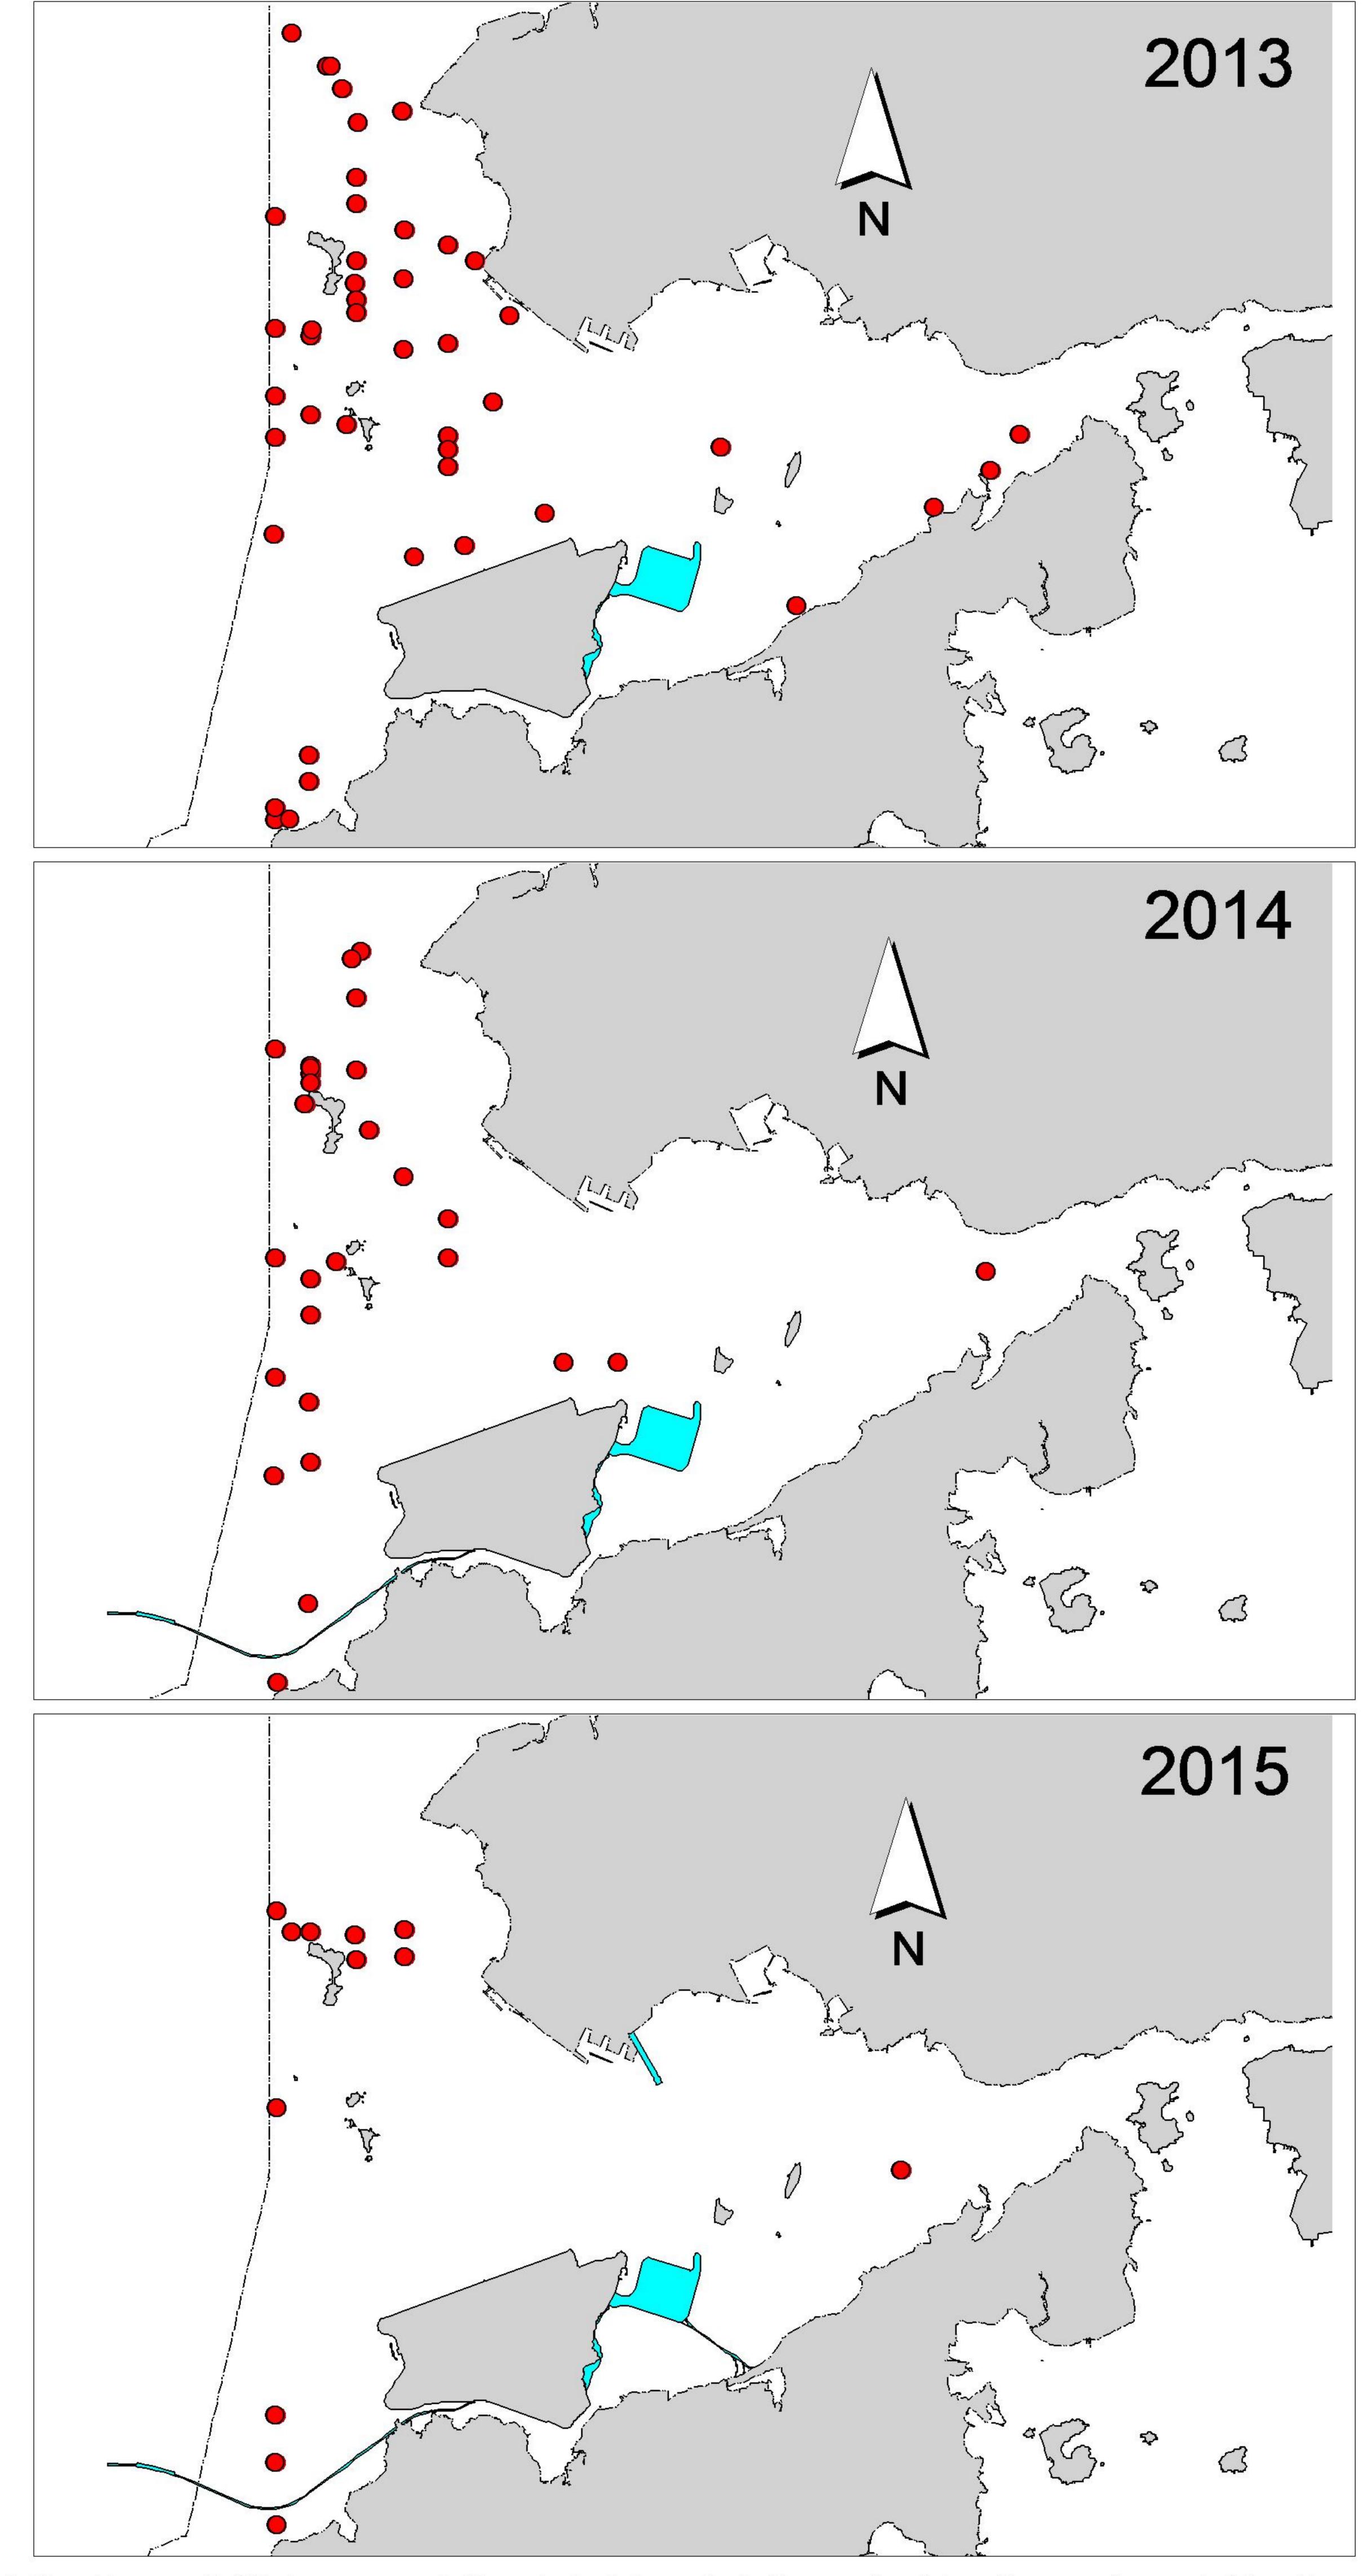
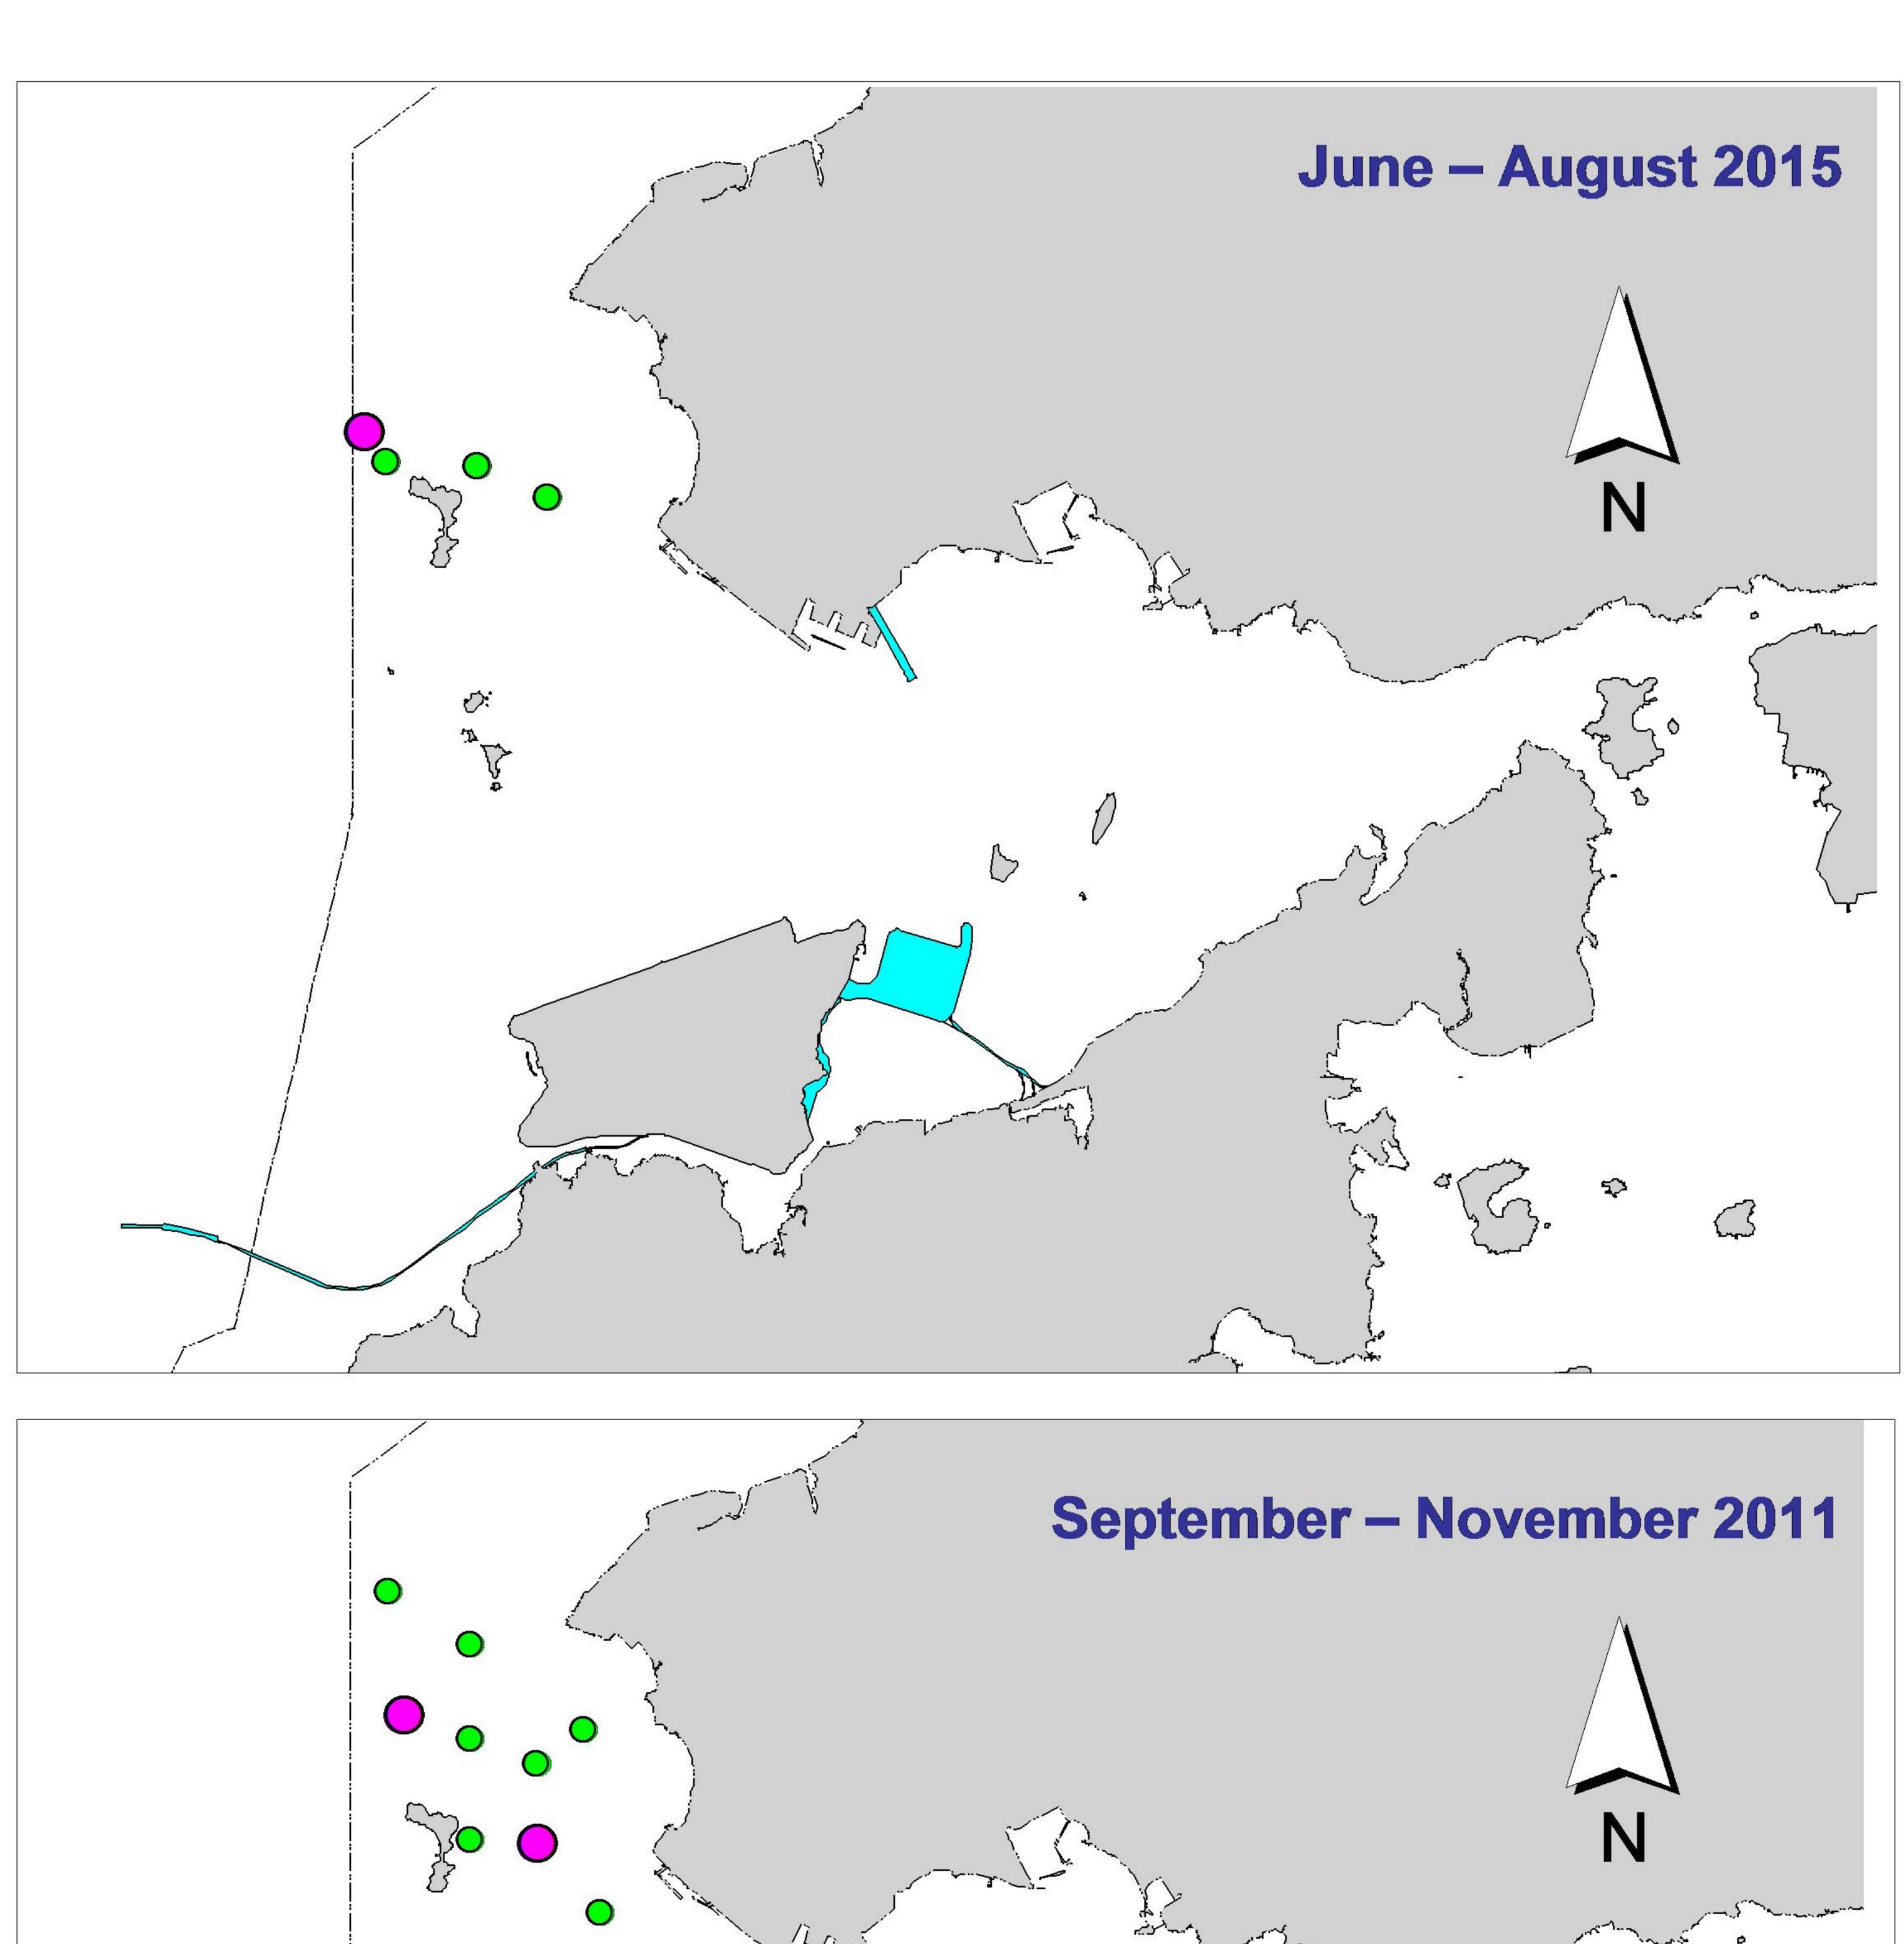


Figure 2. Distribution of Chinese white dolphin sightings in Northwest and Northeast Lantau during the same summer quarters (June-August) of HKLR03 impact phase in 2013-15



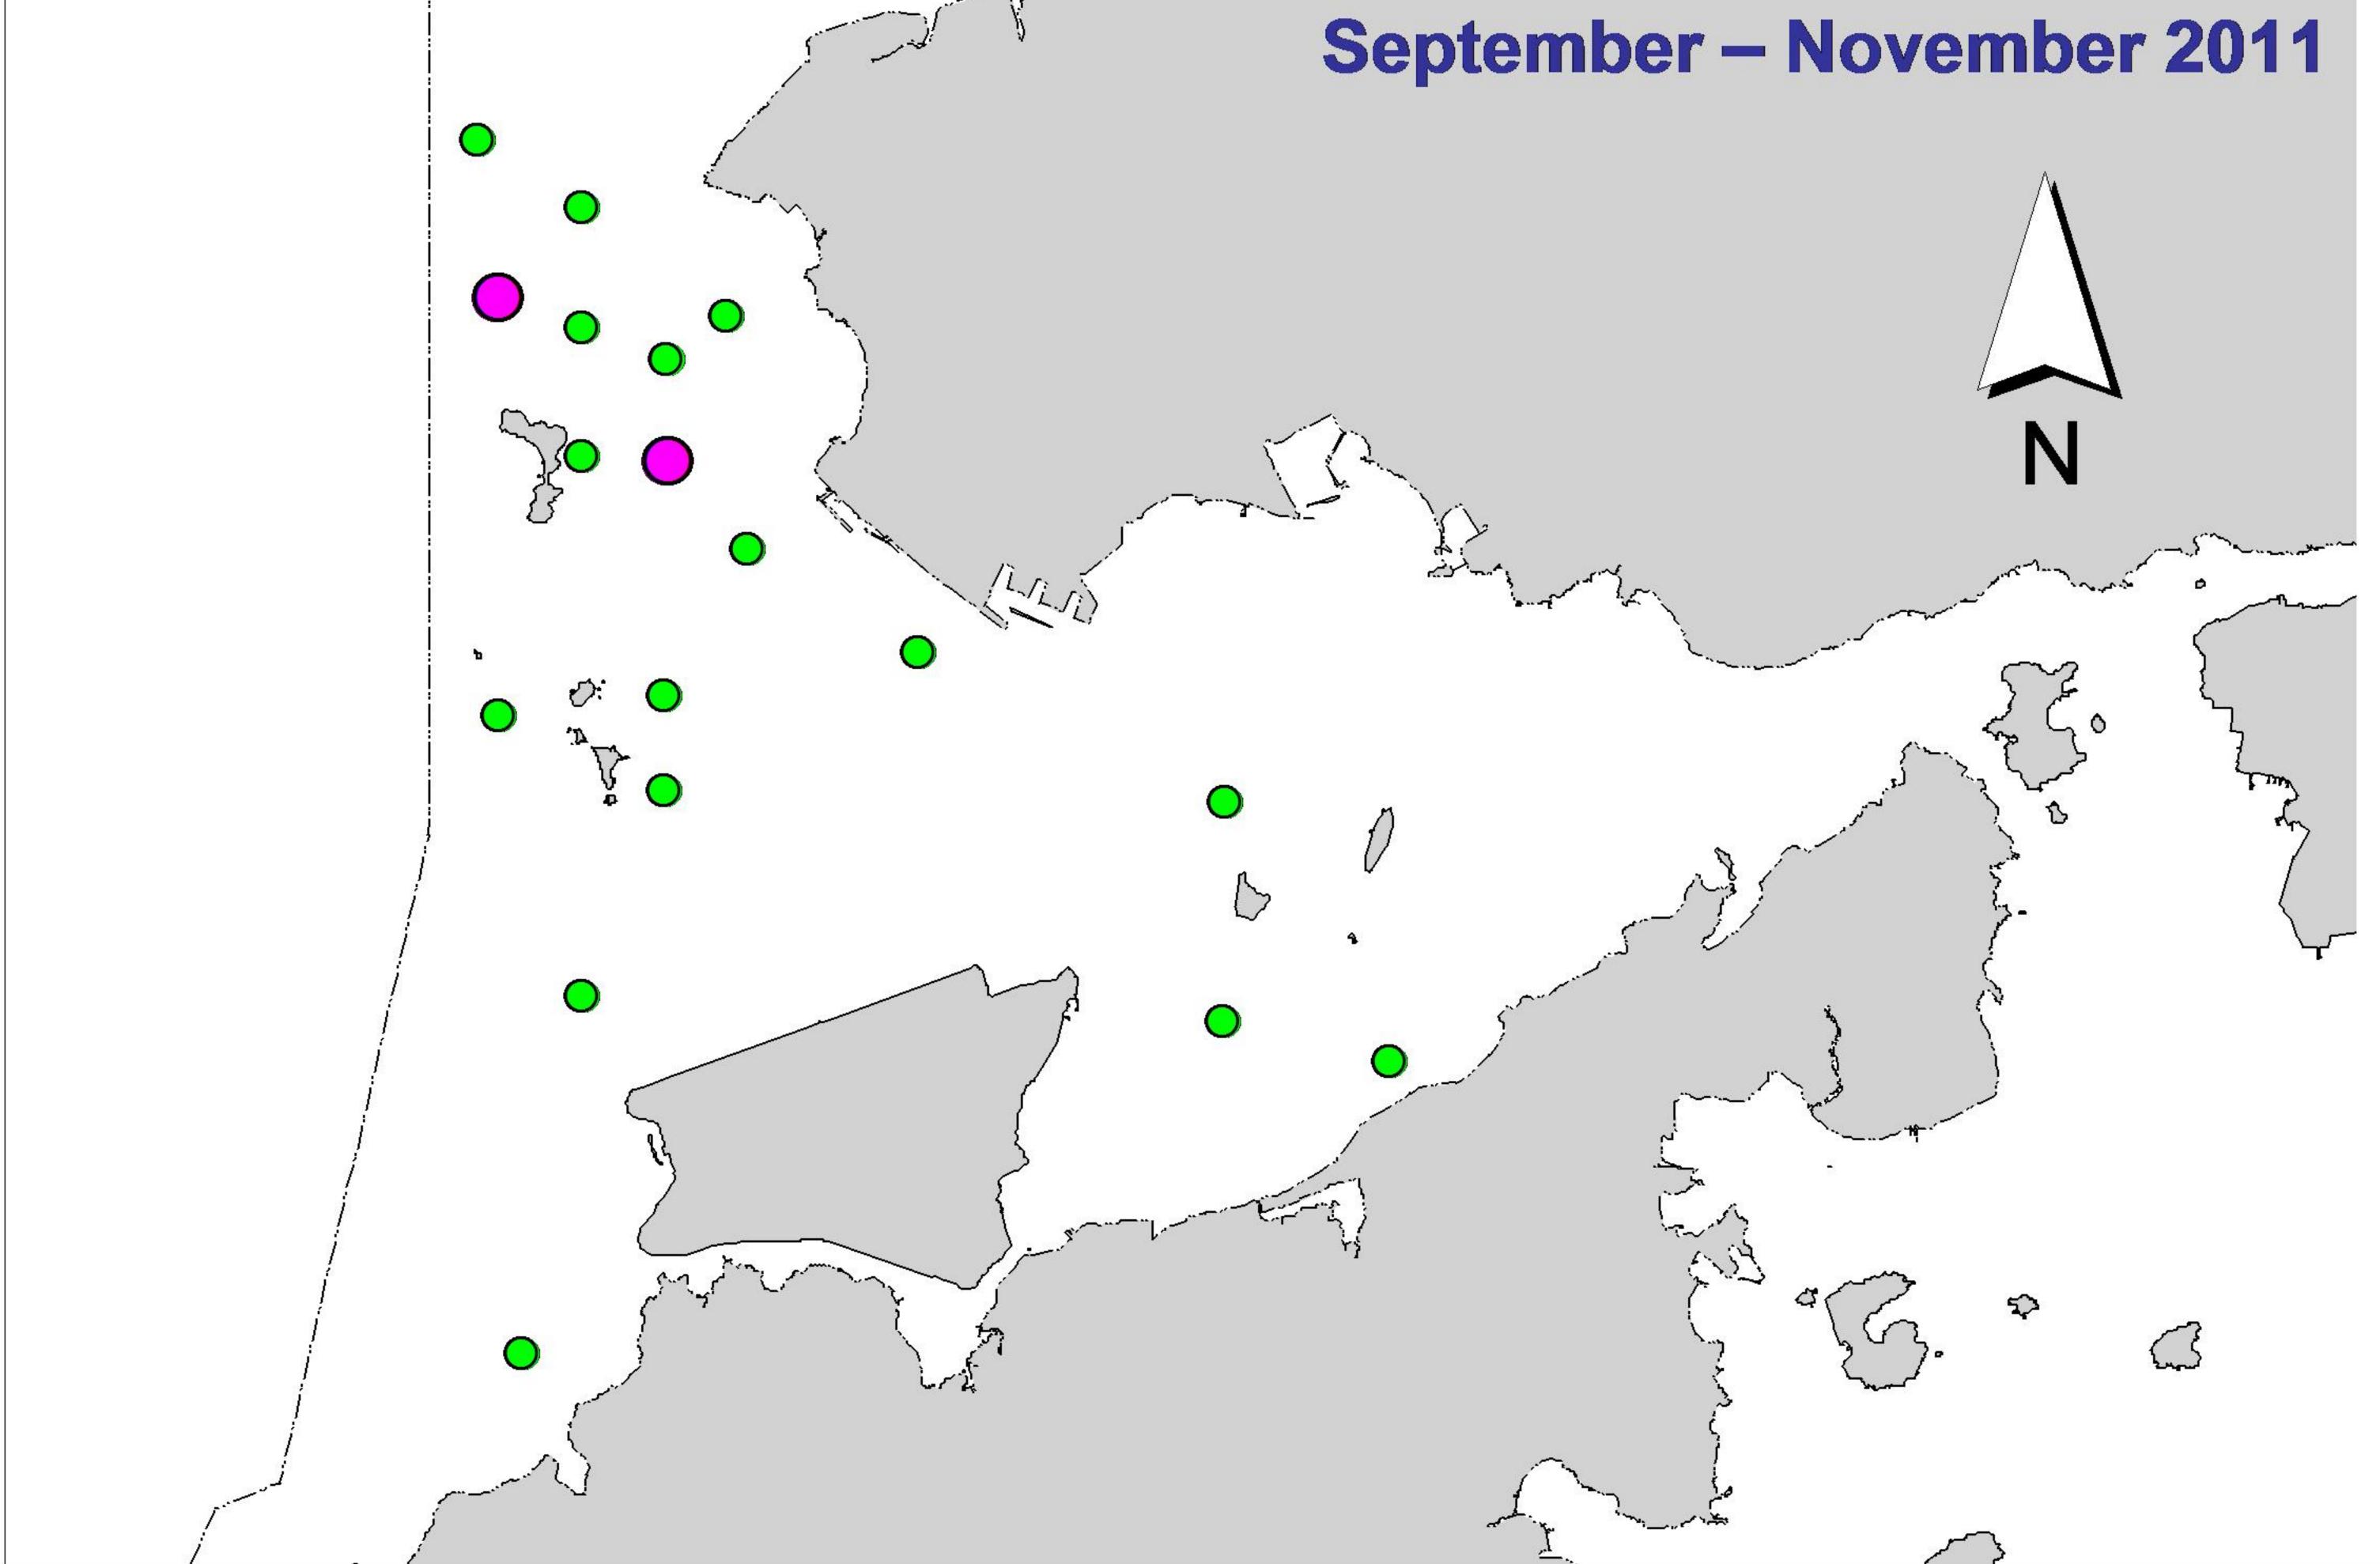


Figure 3. Distribution of Chinese white dolphins with larger group sizes during HKLR03 impact phase (top) and baseline monitoring surveys (bottom) (green dots: group sizes of 5 or more; purple dots: group sizes of 10 or more)

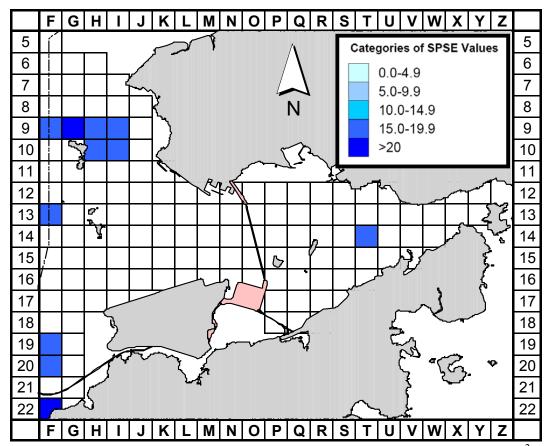


Figure 4a. Sighting density of Chinese white dolphins with corrected survey effort per km² in Northeast and Northwest Lantau survey areas, using data collected during HKLR03 impact monitoring period monitoring period (Jun-Aug 15) (SPSE = no. of on-effort sightings per 100 units of survey effort)

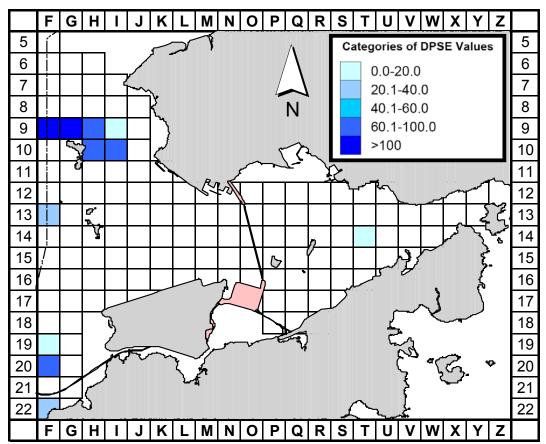


Figure 4b. Density of Chinese white dolphins with corrected survey effort per km² in Northeast and Northwest Lantau survey areas, using data collected during HKLR03 impact monitoring period (Jun-Aug 15) (DPSE = no. of dolphins per 100 units of survey effort)

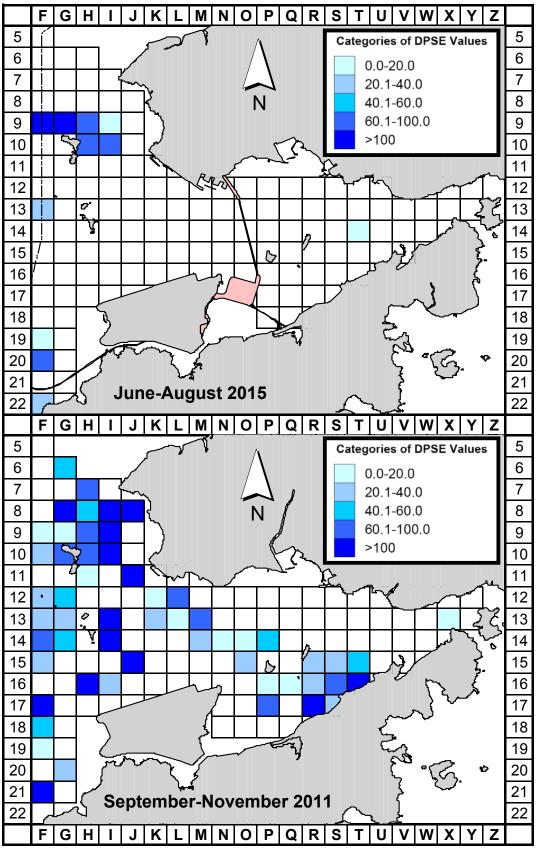


Figure 5. Comparison of density of Chinese white dolphins with corrected survey effort per km² in Northwest and Northeast Lantau survey area between the impact monitoring period (June-August 2015) and baseline monitoring period (September-November 2011) (DPSE = no. of dolphins per 100 units of survey effort)

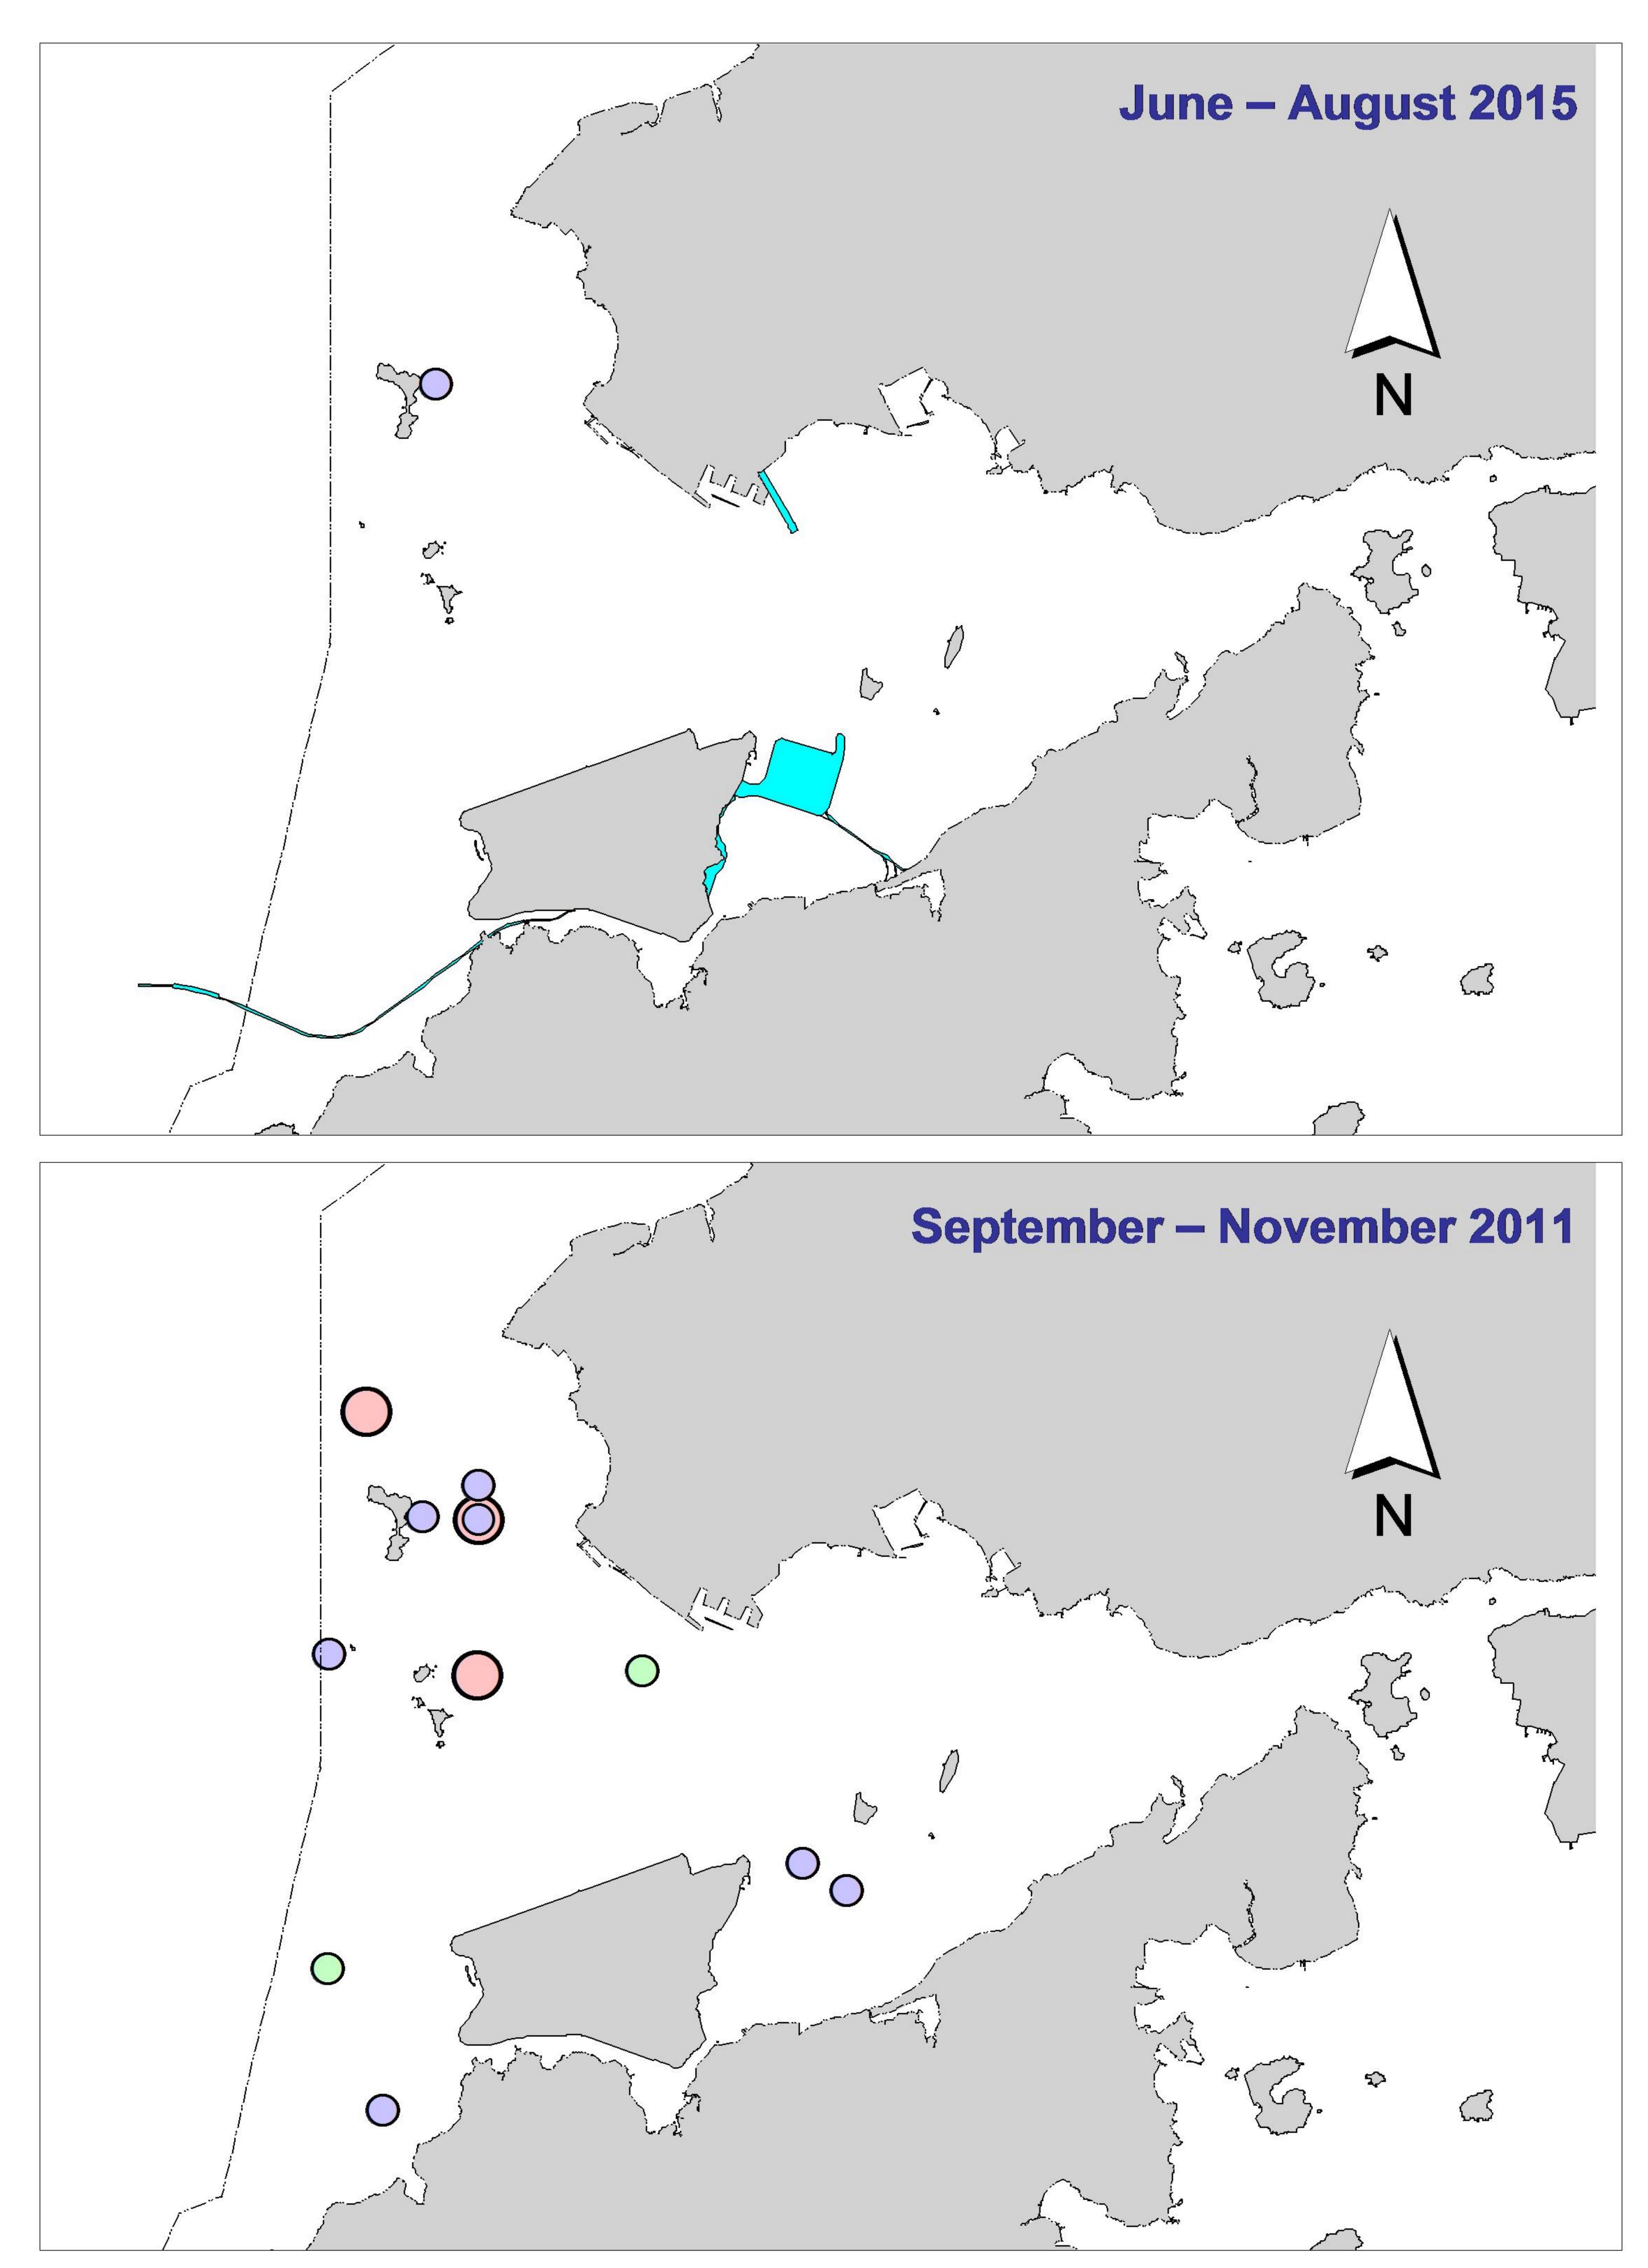


Figure 6. Distribution of Chinese white dolphins engaged in feeding (purple dots), socializing (pink dots) and traveling (green dots) activities during HKLR03 impact phase (top) and baseline monitoring surveys (bottom)

Appendix I. HKLR03 Survey Effort Database (June-August 2015)

(Abbreviations: BEAU = Beaufort Sea State; P = Primary Line Effort; S = Secondary Line Effort)

DATE	AREA	BEAU	EFFORT	SEASON	VESSEL	TYPE	P/S
2-Jun-15	NW LANTAU	2	10.00	SUMMER	STANDARD31516	HKLR	Р
2-Jun-15	NW LANTAU	3	30.49	SUMMER	STANDARD31516	HKLR	Р
2-Jun-15	NW LANTAU	2	7.70	SUMMER	STANDARD31516	HKLR	S
2-Jun-15	NW LANTAU	3	5.61	SUMMER	STANDARD31516	HKLR	S
2-Jun-15	NE LANTAU	2	6.93	SUMMER	STANDARD31516	HKLR	Р
2-Jun-15		3	10.05	SUMMER	STANDARD31516	HKLR	Р
2-Jun-15		2	9.12	SUMMER	STANDARD31516	HKLR	S
2-Jun-15	NE LANTAU	3	0.80	SUMMER	STANDARD31516	HKLR	S
10-Jun-15	NE LANTAU	2	17.06	SUMMER	STANDARD31516	HKLR	P
10-Jun-15	NE LANTAU	3	3.30	SUMMER	STANDARD31516	HKLR	P
10-Jun-15		2	9.14	SUMMER	STANDARD31516	HKLR	S
10-Jun-15		3	1.30	SUMMER	STANDARD31516	HKLR	S
10-Jun-15		2	8.02	SUMMER	STANDARD31516	HKLR	P
10-Jun-15		3	17.50	SUMMER	STANDARD31516	HKLR	Р
10-Jun-15		4	5.86	SUMMER	STANDARD31516	HKLR	Р
10-Jun-15		2	3.48	SUMMER	STANDARD31516	HKLR	S
10-Jun-15	NW LANTAU	3	1.65	SUMMER	STANDARD31516	HKLR	S
10-Jun-15	NW LANTAU	4	2.39	SUMMER	STANDARD31516	HKLR	S
24-Jun-15	NW LANTAU	2	12.10	SUMMER	STANDARD31516	HKLR	P
24-Jun-15		3	19.70	SUMMER	STANDARD31516	HKLR	P
24-Jun-15 24-Jun-15		2	4.80	SUMMER	STANDARD31516	HKLR	S
24-Jun-15 24-Jun-15		3	2.40	SUMMER	STANDARD31516	HKLR	S
24-Jun-15 24-Jun-15		2	20.32	SUMMER	STANDARD31516	HKLR	P
24-Jun-15 24-Jun-15		2	10.68	SUMMER	STANDARD31516	HKLR	S
24-Jun-15 26-Jun-15		3	30.27	SUMMER	STANDARD31516 STANDARD31516	HKLR	o P
26-Jun-15	NW LANTAU	4	10.98	SUMMER	STANDARD31516	HKLR	P
26-Jun-15 26-Jun-15	NW LANTAU	3	6.40	SUMMER	STANDARD31516 STANDARD31516	HKLR	S
26-Jun-15 26-Jun-15		4	6.05	SUMMER	STANDARD31516 STANDARD31516	HKLR	S
	NE LANTAU	2		SUMMER	STANDARD31516 STANDARD31516		o P
26-Jun-15		3	14.33			HKLR	P
26-Jun-15		2	3.16	SUMMER	STANDARD31516 STANDARD31516	HKLR	
26-Jun-15	NE LANTAU	3	6.53	SUMMER	STANDARD31516 STANDARD31516	HKLR	S S
26-Jun-15	NE LANTAU	2	3.18	SUMMER		HKLR	P
2-Jul-15	NW LANTAU	3	1.80	SUMMER	STANDARD31516	HKLR	P P
2-Jul-15	NW LANTAU NW LANTAU	_	29.96 6.90	SUMMER SUMMER	STANDARD31516 STANDARD31516	HKLR HKLR	
2-Jul-15 2-Jul-15	NW LANTAU	4 5	2.30	SUMMER	STANDARD31516 STANDARD31516	HKLR	P P
2-Jul-15 2-Jul-15	NW LANTAU	3	6.30	SUMMER	STANDARD31516	HKLR	S
2-Jul-15	NW LANTAU	4	6.26	SUMMER	STANDARD31516	HKLR	S
2-Jul-15	NE LANTAU	2	14.61	SUMMER	STANDARD31516	HKLR	P
2-Jul-15	NE LANTAU	3	2.80	SUMMER	STANDARD31516	HKLR	P
2-Jul-15	NE LANTAU	2	6.35	SUMMER	STANDARD31516	HKLR	S
2-Jul-15	NE LANTAU	3	3.44	SUMMER	STANDARD31516	HKLR	S
7-Jul-15	NE LANTAU	2	15.85	SUMMER	STANDARD31516	HKLR	P
7-Jul-15	NE LANTAU	3	4.59	SUMMER	STANDARD31516	HKLR	Р
7-Jul-15	NE LANTAU	2	6.60	SUMMER	STANDARD31516	HKLR	S
7-Jul-15	NE LANTAU	3	4.36	SUMMER	STANDARD31516	HKLR	S
7-Jul-15	NW LANTAU	3	27.41	SUMMER	STANDARD31516	HKLR	Р
7-Jul-15	NW LANTAU	4	4.20	SUMMER	STANDARD31516	HKLR	Р
7-Jul-15	NW LANTAU	3	5.89	SUMMER	STANDARD31516	HKLR	S
7-Jul-15	NW LANTAU	4	1.90	SUMMER	STANDARD31516	HKLR	S

Appendix I. (cont'd)

(Abbreviations: BEAU = Beaufort Sea State; P = Primary Line Effort; S = Secondary Line Effort)

DATE	AREA	BEAU	EFFORT	SEASON	VESSEL	TYPE	P/S
22-Jul-15	NW LANTAU	2	17.06	SUMMER	STANDARD31516	HKLR	Р
22-Jul-15	NW LANTAU	3	14.40	SUMMER	STANDARD31516	HKLR	Р
22-Jul-15	NW LANTAU	2	4.32	SUMMER	STANDARD31516	HKLR	S
22-Jul-15	NW LANTAU	3	2.62	SUMMER	STANDARD31516	HKLR	S
22-Jul-15	NE LANTAU	2	14.48	SUMMER	STANDARD31516	HKLR	Р
22-Jul-15	NE LANTAU	3	5.54	SUMMER	STANDARD31516	HKLR	Р
22-Jul-15	NE LANTAU	2	8.78	SUMMER	STANDARD31516	HKLR	S
22-Jul-15	NE LANTAU	3	2.00	SUMMER	STANDARD31516	HKLR	S
27-Jul-15	NW LANTAU	2	1.68	SUMMER	STANDARD31516	HKLR	P
27-Jul-15	NW LANTAU	3	24.69	SUMMER	STANDARD31516	HKLR	Р
27-Jul-15	NW LANTAU	4	14.63	SUMMER	STANDARD31516	HKLR	Р
27-Jul-15	NW LANTAU	2	2.10	SUMMER	STANDARD31516	HKLR	S
27-Jul-15	NW LANTAU	3	8.60	SUMMER	STANDARD31516	HKLR	S
27-Jul-15	NW LANTAU	4	2.50	SUMMER	STANDARD31516	HKLR	S
27-Jul-15	NE LANTAU	2	8.93	SUMMER	STANDARD31516	HKLR	P
27-Jul-15	NE LANTAU	3	7.93	SUMMER	STANDARD31516	HKLR	P
27-Jul-15	NE LANTAU	2	7.74	SUMMER	STANDARD31516	HKLR	S
27-Jul-15	NE LANTAU	3	2.10	SUMMER	STANDARD31516	HKLR	S
10-Aug-15	NW LANTAU	2	19.11	SUMMER	STANDARD31516	HKLR	P
10-Aug-15	NW LANTAU	3	21.29	SUMMER	STANDARD31516	HKLR	Р
10-Aug-15	NW LANTAU	2	7.50	SUMMER	STANDARD31516	HKLR	S
10-Aug-15		3	5.90	SUMMER	STANDARD31516	HKLR	S
10-Aug-15		2	11.97	SUMMER	STANDARD31516	HKLR	P
10-Aug-15		3	4.50	SUMMER	STANDARD31516	HKLR	Р
10-Aug-15		2	8.13	SUMMER	STANDARD31516	HKLR	S
10-Aug-15	NE LANTAU	3	2.10	SUMMER	STANDARD31516	HKLR	S
14-Aug-15	NW LANTAU	1	3.92	SUMMER	STANDARD31516	HKLR	P
14-Aug-15		2	20.74	SUMMER	STANDARD31516	HKLR	Р
14-Aug-15	NW LANTAU	3	7.02	SUMMER	STANDARD31516	HKLR	P
14-Aug-15	NW LANTAU	2	3.00	SUMMER	STANDARD31516	HKLR	S
14-Aug-15	NW LANTAU	3	4.52	SUMMER	STANDARD31516	HKLR	S
14-Aug-15	NE LANTAU	2	18.24	SUMMER	STANDARD31516	HKLR	P
14-Aug-15	NE LANTAU	3	1.90	SUMMER	STANDARD31516	HKLR	Р
14-Aug-15		2	8.36	SUMMER	STANDARD31516	HKLR	S
14-Aug-15	NE LANTAU	3	2.10	SUMMER	STANDARD31516	HKLR	S
19-Aug-15		2	26.22	SUMMER		HKLR	P
19-Aug-15	NW LANTAU		_	SUMMER	STANDARD31516		Р
19-Aug-15 19-Aug-15	NW LANTAU	3 2	12.61 8.42	SUMMER	STANDARD31516 STANDARD31516	HKLR HKLR	
19-Aug-15 19-Aug-15	NW LANTAU		4.39	SUMMER	STANDARD31516 STANDARD31516	HKLR	S S
19-Aug-15 19-Aug-15		3			STANDARD31516 STANDARD31516		P
	NE LANTAU	2	16.55	SUMMER		HKLR	
19-Aug-15	NE LANTAU	2	9.95 1.65	SUMMER	STANDARD31516	HKLR	S
28-Aug-15	NE LANTAU	1	1.65	SUMMER	STANDARD31523	HKLR	Р
28-Aug-15	NE LANTAU	2	17.34	SUMMER	STANDARD31524	HKLR	Р
28-Aug-15	NE LANTAU	1	3.09	SUMMER	STANDARD31525	HKLR	S
28-Aug-15	NE LANTAU	2	7.70	SUMMER	STANDARD31526	HKLR	S
28-Aug-15	NW LANTAU	2	16.74	SUMMER	STANDARD31527	HKLR	Р
28-Aug-15	NW LANTAU	3	14.81	SUMMER	STANDARD31528	HKLR	Р
28-Aug-15	NW LANTAU	4	1.30	SUMMER	STANDARD31529	HKLR	Р
28-Aug-15	NW LANTAU	2	6.65	SUMMER	STANDARD31530	HKLR	S

Appendix II. HKLR03 Chinese White Dolphin Sighting Database (June-August 2015)

(Abberviations: STG# = Sighting Number; HRD SZ = Dolphin Herd Size; BEAU = Beaufort Sea State; PSD = Perpendicular Distance; BOAT ASSOC. = Fishing Boat Association, P/S: Sighting Made on Primary/Secondary Lines)

DATE	STG#	TIME	HRD SZ	AREA	BEAU	PSD	EFFORT	TYPE	NORTHING	EASTING	SEASON	BOAT ASSOC.	P/S
2-Jun-15	1	1110	10	NW LANTAU	3	88	ON	HKLR	827673	804687	SUMMER	NONE	Р
26-Jun-15	1	1210	4	NW LANTAU	4	357	ON	HKLR	826650	806456	SUMMER	NONE	Р
26-Jun-15	2	1610	1	NE LANTAU	2	0	ON	HKLR	822224	818562	SUMMER	NONE	Р
2-Jul-15	1	1051	2	NW LANTAU	3	158	ON	HKLR	823542	804688	SUMMER	NONE	Р
22-Jul-15	1	1055	3	NW LANTAU	3	153	ON	HKLR	827217	805458	SUMMER	NONE	Р
22-Jul-15	2	1140	1	NW LANTAU	3	147	ON	HKLR	827280	807549	SUMMER	NONE	Р
19-Aug-15	1	1019	1	NW LANTAU	2	45	ON	HKLR	814805	804681	SUMMER	NONE	Р
19-Aug-15	2	1031	4	NW LANTAU	2	502	ON	HKLR	816101	804673	SUMMER	NONE	Р
19-Aug-15	3	1036	1	NW LANTAU	2	285	ON	HKLR	817097	804675	SUMMER	NONE	Р
19-Aug-15	4	1125	5	NW LANTAU	2	733	ON	HKLR	827218	805036	SUMMER	NONE	Р
19-Aug-15	5	1221	5	NW LANTAU	2	98	ON	HKLR	827182	806436	SUMMER	NONE	Р
28-Aug-15	1	1417	5	NW LANTAU	3	344	ON	HKLR	826693	807538	SUMMER	NONE	Р

Appendix III. Individual dolphins identified during HKLR03 monitoring surveys in June-August 2015

ID#	DATE	STG#	AREA
CH34	02/06/15	1	NW LANTAU
	28/08/15	1	NW LANTAU
NL37	02/06/15	1	NW LANTAU
NL46	19/08/15	4	NW LANTAU
NL48	02/06/15	1	NW LANTAU
NL104	02/06/15	1	NW LANTAU
	19/08/15	4	NW LANTAU
	28/08/15	1	NW LANTAU
NL136	02/06/15	1	NW LANTAU
	28/08/15	1	NW LANTAU
NL153	19/08/15	5	NW LANTAU
NL182	02/06/15	1	NW LANTAU
NL202	02/06/15	1	NW LANTAU
	26/06/15	1	NW LANTAU
	19/08/15	5	NW LANTAU
NL213	26/06/15	1	NW LANTAU
NL214	28/08/15	1	NW LANTAU
NL220	28/08/15	1	NW LANTAU
NL233	22/07/15	1	NW LANTAU
NL286	02/06/15	1	NW LANTAU
	26/06/15	1	NW LANTAU
	19/08/15	5	NW LANTAU
NL293	19/08/15	1	NW LANTAU
NL310	02/07/15	1	NW LANTAU
	19/08/15	4	NW LANTAU
NL319	26/06/15	1	NW LANTAU
WL05	02/06/15	1	NW LANTAU
WL17	19/08/15	4	NW LANTAU
WL124	19/08/15	3	NW LANTAU
WL167	02/07/15	1	NW LANTAU

Appendix IV. Twenty-one individual dolphins that were identified during June – August 2015 under HKLR03 impact phase monitoring surveys



Appendix IV. (cont'd)



Appendix IV. (cont'd)



Appendix IV. (cont'd)




Appendix IV. (cont'd)




Appendix IV. (cont'd)




Appendix V. Ranging patterns (95% kernel ranges) of 21 individual dolphins that were sighted during HKLR03 impact phase monitoring period (note: yellow dots indicates sightings made in June – August 2015)

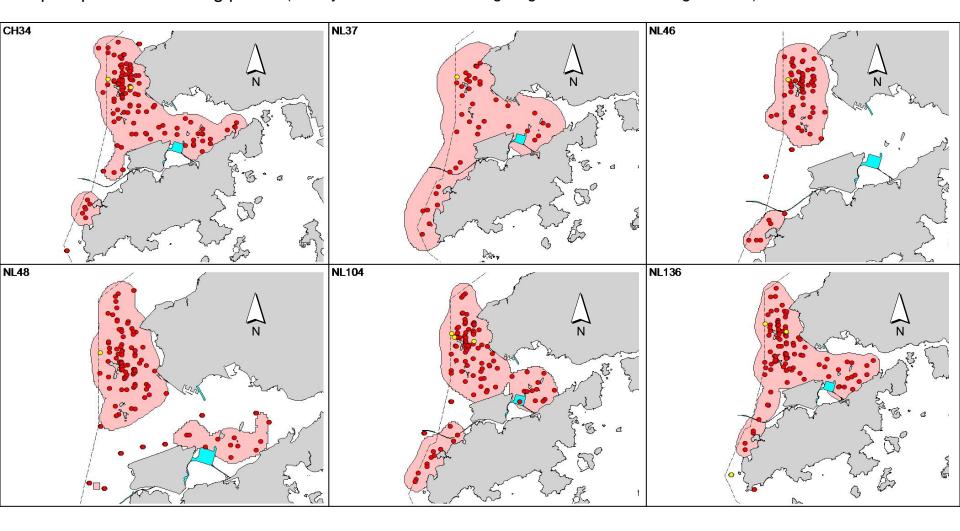


Appendix V. (cont'd)

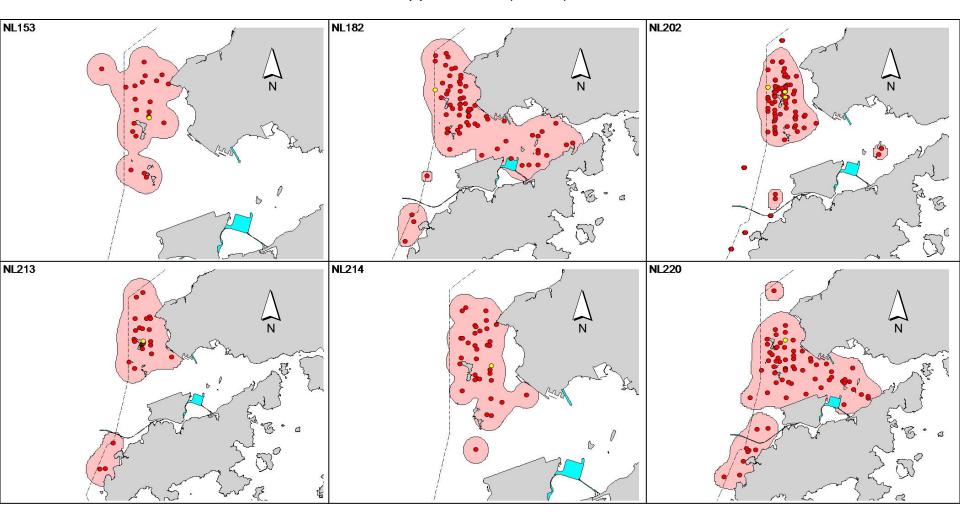

Appendix V. (cont'd)

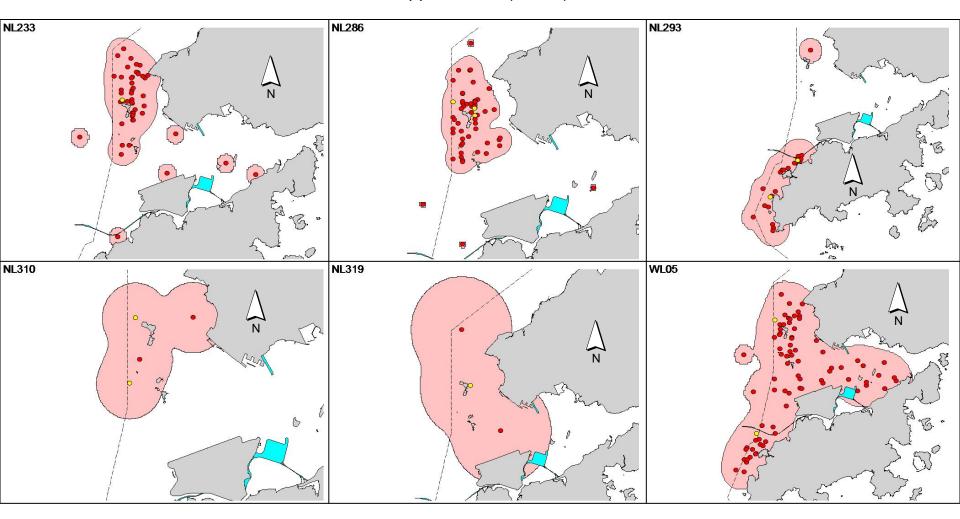

Appendix V. (cont'd)

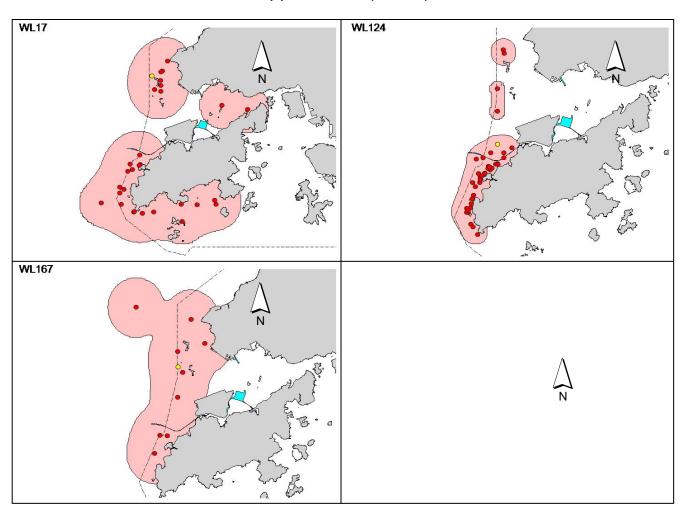

Appendix I

Event and Action Plan

Event and Action Plan for Impact Air Monitoring

			Action				
	ET (a)		IEC (a)		SOR (a)		Contractor(s)
Action Level							
Exceedance recorded 1. 2.	Identify the source. Repeat measurement to confirm finding. If two consecutive measurements exceed Action Level, the	 1. 2. 	Check monitoring data submitted by the ET. Check the Contractor's	1.	Confirm receipt of notification of failure in writing.	1.	Rectify any unacceptable practice Amend working
3. 4.	exceedance is then confirmed. Inform the IEC and the SOR. Investigate the cause of exceedance and check	3.	working method. If the exceedance is confirmed to be Project	2. 3.	Notify the Contractor. Ensure remedial measures properly implemented.	3.	methods if appropriate If the exceedance is confirmed to be Project
_	Contractor's working procedures to determine possible mitigation to be implemented.		related after investigation, discuss with the ET and the				related, submit proposals for remedial
5. 6.	If the exceedance is confirmed to be Project related after investigation, increase monitoring frequency to daily. Discuss with the IEC and the Contractor on remedial	4.	Contractor on possible remedial measures. Advise the SOR on the				actions to IEC within 3 working days of notification
7.	actions required. If exceedance continues, arrange meeting with the IEC		effectiveness of the proposed remedial measures.			4.	Implement the agreed proposals
8.	and the SOR. If exceedance stops, cease additional monitoring.	5.	Supervisor implementation of remedial measures.			5.	Amend proposal if appropriate

		Action		
	ET (a)	IEC (a)	SOR (a)	Contractor(s)
Limit Level				
Limit Level Exceedance recorded	 Identify the source. Repeat measurement to confirm finding. two consecutive measurements exceed Li Level, the exceedance is then confirmed. Inform the IEC, the SOR, the DEP and the Contractor. Investigate the cause of exceedance and check Contractor's working procedures to determine possible mitigation to be implemented. If the exceedance is confirmed to be Projected after investigation, increase monitoring frequency to daily. Carry out analysis of the Contractor's working procedures to determine possible mitigation to be implemented. Arrange meeting with the IEC and the SO to discuss the remedial actions to be taken. Assess effectiveness of the Contractor's remedial actions and keep the IEC, the Diand the SOR informed of the results. 	imit 2. Check Contractor's working method. e 3. If the exceedance is confirmed to be Project related after investigation, discuss with the ET and the Contractor on possible remedial measures. ect 4. Advise the SOR on the effectiveness of the proposed remedial measures. 5. Supervisor implementation of remedial measures. OR on.	 Notify the Contractor. If the exceedance is confirmed to be Project related after investigation, in consultation with the IEC, agree with the Contractor on the remedial measures to be implemented. 	proposals for remedia
	If exceedance stops, cease additional monitoring.			

Note: (a) ET - Environmental Team; IEC - Independent Environmental Checker; SOR - Supervising Officer's Representative

Event & Action Plan for Water Quality

Event	ET I	Leader	IEC		SOR			Contractor		
Action level being exceeded by one sampling day	 2. 3. 4. 	Repeat <i>in situ</i> measurement on next day of exceedance to confirm findings; Identify source(s) of impact; Inform IEC, contractor and SOR; Check monitoring data, all plant, equipment and Contractor's working methods.	1.	Check monitoring data submitted by ET and Contractor's working methods.	2.	Confirm receipt of notification of non-compliance in writing; Notify Contractor.	 2. 3. 	Inform the SOR and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Amend working methods if appropriate.		
Action level being exceeded by two or more consecutive sampling days	 2. 3. 4. 6. 7. 	Repeat measurement on next day of exceedance to confirm findings; Identify source(s) of impact; Inform IEC, contractor, SOR and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, SOR and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Action level;	 2. 3. 	Check monitoring data submitted by ET and Contractor's working method; Discuss with ET and Contractor on possible remedial actions; Review the proposed mitigation measures submitted by Contractor and advise the SOR accordingly; Supervise the implementation of mitigation measures.	 2. 3. 	Discuss with IEC on the proposed mitigation measures; Ensure mitigation measures are properly implemented; Assess the effectiveness of the implemented mitigation measures.	 2. 3. 4. 	Inform the Supervising Officer and confirm notification of the non- compliance in writing; Rectify unacceptable practice; Check all plant and equipment and consider changes of working methods; Submit proposal of additional mitigation measures to SOR within 3 working days of notification and discuss with ET, IEC and SOR; Implement the agreed mitigation measures.		
Limit level being exceeded by one sampling day	1.	Repeat measurement on next day of exceedance to confirm findings;	1.	Check monitoring data submitted by ET and	1.	Confirm receipt of notification of failure in	1.	Inform the SOR and confirm notification of the		

Event	ET Leader	IEC	SOR	Contractor
	 Identify source(s) of impact; Inform IEC, contractor, SOR and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, SOR and Contractor; 	Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the SOR accordingly.	 writing; Discuss with IEC, ET and Contractor on the proposed mitigation measures; Request Contractor to review the working methods. 	non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Submit proposal of mitigation measures to SOR within 3 working days of notification and discuss with ET, IEC and SOR.
Limit level being exceeded by two or more consecutive sampling days	 Repeat measurement on next day of exceedance to confirm findings; Identify source(s) of impact; Inform IEC, contractor, SOR and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC, SOR and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days; 	 Check monitoring data submitted by ET and Contractor's working method; Discuss with ET and Contractor on possible remedial actions; Review the Contractor's mitigation measures whenever necessary to assure their effectiveness and advise the SOR accordingly; Supervise the implementation of mitigation measures. 	are properly implemented;Consider and instruct, if	 Take immediate action to avoid further exceedance; Submit proposal of mitigation measures to SOR within 3 working days of notification and discuss with ET, IEC and SOR; Implement the agreed mitigation measures; Resubmit proposals of mitigation measures if problem still not under control; As directed by the Supervising Officer, to slow down or to stop all or part of the construction activities until no exceedance of Limit level.

Note: ET – Environmental Team, IEC – Independent Environmental Checker, SOR – Supervising Officer's Representative

Event/Action Plan for Impact Dolphin Monitoring

EVENT	ACTION*							
	ET	IEC	SOR	Contractor				
Action Level	 Repeat statistical data analysis to confirm findings; Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; Identify source(s) of impact; Inform the IEC, SOR and Contractor; Check monitoring data. Review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary. 	 Check monitoring data submitted by ET and Contractor; Discuss monitoring results and finding with the ET and the Contractor. 	 Discuss monitoring with the IEC and any other measures proposed by the ET; If SOR is satisfied with the proposal of any other measures, SOR to signify the agreement in writing on the measures to be implemented. 	 Inform the SOR and confirm notification of the non-compliance in writing; Discuss with the ET and the IEC and propose measures to the IEC and the SOR; Implement the agreed measures. 				
Limit Level	 Repeat statistical data analysis to confirm findings; Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 	 Check monitoring data submitted by ET and Contractor; Discuss monitoring results and findings with the ET and the Contractor; Attend the meeting to discuss with ET, SOR and 	 Attend the meeting to discuss with ET, IEC and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures. If SOR is satisfied with the 	 Inform the SOR and confirm notification of the non-compliance in writing; Attend the meeting to discuss with ET, IEC and SOR the necessity of additional dolphin monitoring and any other 				

EVENT	ACTION*								
	ET	IEC	SOR	Contractor					
	 Identify source(s) of impact; Inform the IEC, SOR and Contractor of findings; Check monitoring data; Repeat review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary. If ET proves that the source of impact is caused by any of the construction activity by the works contract, ET to arrange a meeting to discuss with IEC, SOR and Contractor the necessity of additional dolphin monitoring and/or any other potential mitigation measures (e.g., consider to modify the perimeter silt curtain or consider to control/temporarily stop relevant construction activity etc.) and submit to IEC a proposal of additional dolphin monitoring and/or mitigation measures where necessary. 	Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures. 4. Review proposals for additional monitoring and any other mitigation measures submitted by ET and Contractor and advise SOR of the results and findings accordingly. 5. Supervise / Audit the implementation of additional monitoring and/or any other mitigation measures and advise SOR the results and findings accordingly.	proposals for additional dolphin monitoring and/or any other mitigation measures submitted by ET and Contractor and verified by IEC, SOR to signify the agreement in writing on such proposals and any other mitigation measures. 3. Supervise the implementation of additional monitoring and/or any other mitigation measures.	potential mitigation measures. 3. Jointly submit with ET to IEC a proposal of additional dolphin monitoring and/or any other mitigation measures when necessary. 4. Implement the agreed additional dolphin monitoring and/or any other mitigation measures.					

Appendix J

Cumulative Statistics on Exceedances, Complaints, Notifications of Summons and Successful Prosecutions

Table J1 Cumulative Statistics on Exceedances

Monitoring Parameters	Action/Limit Level	Total No. recorded in this reporting quarter	Total No. recorded since project commencement
1-Hr TSP	Action	0	30
	Limit	0	2
24-Hr TSP	Action	0	5
	Limit	0	1
Water Quality	Action	0	6
	Limit	0	1
Impact Dolphin	Action	0	7
Monitoring	Limit	1	3

Table J2 Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Reporting Period		Cumulative Statistics	
_	Complaints	Notifications of	Successful
		Summons	Prosecutions
This Reporting Period	0	0	0
(June 2015 to August			
2015)			
Total No. received	4	0	0
since project			
commencement			

Email message

From

Environmental Resources Management

To Ramboll Environ - Hong Kong, Limited (ENPO)

ERM- Hong Kong, Limited

16/F Berkshire House, 25 Westlands Road Quarry Bay, Hong Kong Telephone: (852) 2271 3113 Facsimile: (852) 2723 5660 E-mail: jovy.tam@erm.com

Ref/Project number Contract No. HY/2012/08 Tuen Mun-Chek Lap

Kok Link-Northern Connection Sub-sea Tunnel

Section

Subject Notification of Exceedance for Impact Dolphin

Monitoring

Date 4 November 2015



Dear Sir or Madam,

Please find attached the Notification of Exceedance (NOE) of the following Log no.:

 $0212330_Jun2015/Aug2015_dolphin_STG\&ANI_NEL\&NWL$

A total of one limit level exceedance was recorded in the quarterly impact dolphin monitoring data between June 2015 and August 2015.

Regards,

Mr Jovy Tam

Environmental Team Leader

CONFIDENTIALITY NOTICE

This facsimile transmission is intended only for the use of the addressee and is confidential. If you are not the addressee it may be unlawful for you to read, copy, distribute, disclose or otherwise use the information in this facsimile. If you are not the intended recipient, please telephone or fax us.



ERM-Hong Kong, Limited

CONTRACT NO. HY/2012/08 TUEN MUN - CHEK LAP KOK LINK NORTHERN CONNECTION SUB-SEA TUNNEL SECTION

Impact Dolphin Monitoring Notification of Exceedance

Log No.	0212330_Jun2015/Aug2015_dolphin_STG&ANI_NEL&NWL					
	[Total No. of Exceedances = 1 Limit Level Exceedance]					
Date	June 2015 to August 2015 (monitored)					
	24 September 2015 (results received by ERM)					
Monitoring Area	Northeast L	antau (NEL) and Northwest Lantau (NWL)				
Parameter(s) with	Quarterly	encounter rate of dolphin sightings (STG)				
Exceedance(s)		counter rate of total number of dolphins (ANI)				
Action Levels		NEL: STG < 4.2 & ANI < 15.5				
		or				
	North Lantau Social cluster	NWL: STG < 6.9 & ANI < 31.3				
Limit Levels	North Lantau Social Cluster	NEL: STG < 2.4 & ANI < 8.9				
		and				
		NWL: STG < 3.9 & ANI < 17.9				
Recorded Levels	NEL	STG = 0.44 & ANI = 0.44				
	NWL	STG = 2.53 & ANI = 9.21				
	One Limit Level Exceedance is recorded in the quarterly impact dolphin monitoring at NEL and NWL between June 2015 and August 2015. The exceedance was reported in the approved Twenty-second <i>Monthly EM&A Report</i> dated 14 September 2015.					
Statistical Analyses	 Further to the review of the available and relevant dolphin monitoring data in the EM&A programme by this Contract, statistical analyses were conducted as follows: A two-way ANOVA with repeated measures and unequal sample size was conducted using Period (2 levels: baseline vs impact – present quarter, June 2015 to August 2015) and Location (2 levels: NEL and NWL) as fixed factors to examine whether there were any significant differences in the averages encounter rates between the baseline and present impact monitoring quarter. By setting α = 0.05 as the significance level in the statistical tests, significant difference in STG (<i>p</i> = 0.0064) and in ANI (<i>p</i> = 0.0270) between Period were detected. A two-way ANOVA with repeated measures and unequal sample size was conducted using Cumulative Period (2 levels: baseline vs impact – cumulative quarters*, December 2012 to August 2015) and Location (2 levels: NEL and NWL) as fixed factors to examine whether there were any significant differences in the averages encounter rates between the baseline and cumulative impact monitoring quarters. By setting α = 0.01 as the significance level in the statistical tests, significant difference in STG (<i>p</i> = 0.00020) and in ANI (<i>p</i> = 0.00005) between Cumulative Period and Location were detected. *Note: The commencement date under <i>Contract No. HY/2012/08</i> is 1 November 2013. 					
Works Undertaken (in the monitoring quarter)	In the quarter between June 2015 a Contract.	and August 2015, no marine works was carried out in this				

Possible Reason for	The exceedance is considered not caused by the Project, in view of the following:
Action or Limit Level	The Monitoring of Marine Mammals in Hong Kong Waters (2014 – 15) (1) reported that dolphin
Exceedance(s)	 usage and traveling activities to the northern side of the airport (dolphin traveling corridor) are affected by frequent high-speed ferry traffic from Sky Pier (not related to this project), which is likely a contributing factor for the decrease in dolphin abundances in NEL. As per the findings from the EIA report (Section 8.11.9), the major influences on the Chinese White Dolphin (CWD) are marine traffics, dredging works and reclamation/filling works. The Contractor has implemented the marine traffic control as per the requirements in the EP-354/2009/D and the updated EM&A Manual. No marine works were carried out during the monitoring quarter. During this quarter of dolphin monitoring, no unacceptable impact on CWD due to the activities under this Contract was observed.
Actions Taken / To Be	With reference to the site inspection records in this quarter, the respective marine ecological
Taken	mitigation measures (including marine traffic control) have been implemented properly by the Contractor throughout the marine works period. No immediate additional action is considered necessary. The ET will monitor for future trends in exceedance(s). A joint team meeting was held on 6 October 2015 for discussion on CWD trend, with attendance of ENPO, HyD, Representatives of Resident Site Staff (RSS), Environmental Team (ET) for Contract No. HY/2010/02, HY2011/03, HY/2012/07 and HY/2012/08, and Representatives of Main Contractor for Contract No. HY/2012/07 and HY/2012/08. The discussion/recommendation as recorded in the minutes of the meeting, which might be relevant to this Contract are summarized below. It was concluded that the HZMB works is one of the contributing factors affecting the dolphins. It was also concluded the contribution of impacts due to the HZMB works as a whole (or individual marine contracts) cannot be quantified nor separate from the other stress factors. It was reminded that the ETs shall keep reviewing the implementation status of the dolphin related mitigation measures and remind the contractor to ensure the relevant measures were fully implemented. The participants were requested by ENPO to collect and report the marine traffic statistics. It was recommended that the marine works of HZMB projects should be completed as soon as possible so as to reduce the overall duration of impacts and allow the dolphins population to recover as early as possible.
Remarks	The results of impact water quality and impact dolphin monitoring, the status of implemented marine ecological mitigation measures are documented in the approved <i>Twentieth</i> to <i>Twenty-second EM&A Monthly Reports</i> .

Appendix K

Waste Flow Table



Monthly Summary Waste Flow Table

Name of Department: HyD Contract No. / Works Order No.: HY/2012/08

Monthly Summary Waste Flow Table for August 2015 [to be submitted not later than the 15th day of each month following reporting month] (All quantities shall be rounded off to 3 decimal places.)

	Monthly Break-down of <u>Inert</u> Construction & Demolition Materials (i.e. Public Fill Materials)						
Month	(a)=(b)+(c)+(d)+(e) Total Quantity Generated	(b) Hard Rock and Large Broken Concrete	(c) Reused in the Contract	(d) Reused in other Projects	(e) Disposed of as Public Fill		
	(in '000 ton)	(in '000 ton)	(in '000 ton)	(in '000 ton)	(in '000 ton)		
Sub-total	64.216	0.000	0.000	0.000	64.216		
Jan-2015	30.877	0.000	0.000	0.000	30.877		
Feb-2015	4.152	0.000	0.000	0.000	4.152		
Mar-2015	36.718	0.000	0.000	0.000	36.718		
Apr-2015	62.847	0.000	0.000	0.000	62.847		
May-2015	121.436	0.000	0.000	0.000	121.436		
Jun-2015	247.282	0.000	0.000	0.000	247.282		
Half Year Sub-total	503.312	0.000	0.000	0.000	503.312		
Jul-2015	233.422	0.000	0.000	0.000	233.422		
Aug-2015	62.367	0.000	0.000	0.000	62.367		
Sep-2015							
Oct-2015							
Nov-2015							
Dec-2015							
Project Total Quantities	863.317	0.000	0.000	0.000	863.317		

		Actual Quantities of Non-inert Construction Waste Generated Monthly							
Month	Metals Paper/ ca		Paper/ cardbo	Paper/ cardboard packaging		Plastics (see Note 3)		al Waste	Others, e.g. General Refuse disposed at Landfill
	(in '0	000kg)	(in '(000kg)	(in '(000kg)	(in '0	00kg)	(in '000ton)
	generated	recycled	generated	recycled	generated	recycled	generated	Disposed	generated
Sub-total	0.000	0.000	1.050	1.050	0.000	0.000	0.110	0.110	0.605
Jan-2015	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.080
Feb-2015	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.074
Mar-2015	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.115
Apr-2015	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.091
May-2015	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.108
Jun-2015	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.120
Half Year Sub-total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.588
Jul-2015	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.172
Aug-2015	0.000	0.000	0.000	0.300	0.000	0.000	0.000	0.000	0.246
Sep-2015									
Oct-2015									
Nov-2015									
Dec-2015									
Project Total Quantities	0.000	0.000	1.050	1.350	0.000	0.000	0.110	0.110	1.611



Forecast of Total Quantities of Construction and Demolition Materials to be Generated from the Contract*						
Total Quantity Generated Hard Rock and Large Broken Concrete Reused in the Contract Reused in other Projects Disposed of as Public Fill						
(in '000 ton) (in '000 ton) (in '000 ton) (in '000 ton)						
100.000 0.000 0.000 100.000						

Forecast of Total Quantities of Construction and Demolition Materials to be Generated from the Contract*						
Metals	Metals Paper/ cardboard packaging Plastics (see Note 3) Chemical Waste General Refuse disposed of at Landfill					
(in '000kg)	(in '000kg)	(in '000kg) (in '000kg) (in '000kg) (in '000m³)				
0.000	0.000 0.000 0.000 0.200					

Notes:

- (1) The performance targets are given in the **ER Appendix 8J Clause 14** and the EM & A Manual(s).
- (2) The waste flow table shall also include C&D materials to be imported for use at the Site.
- (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.
- The Contractor shall also submit the latest forecast of the total amount of C&D materials expected to be generated from the Works, together with a breakdown of the nature where the amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000 m³. (ER Part 8 Clause 8.8.5 (d) (ii) refers).
