



**AUES JOB No.: TCS00715/14**

**TUEN MUN - CHEK LAP KOK LINK  
CONTRACT NO. HY/2013/12 –  
NORTHERN CONNECTION TOLL PLAZA AND  
ASSOCIATED WORKS**

**37<sup>TH</sup> MONTHLY ENVIRONMENTAL MONITORING AND  
AUDIT (EM&A) REPORT – NOVEMBER 2017**

PREPARED FOR  
**CRBC AND KADEN JOINT VENTURE**

<b>Date</b>	<b>Reference No.</b>	<b>Prepared By</b>	<b>Certified By</b>
13 December 2017	TCS00715/14/600/R0360v2	 Ben Tam (Environmental Consultant)	 T.W. Tam (Environmental Team Leader)

Ref.: HYDHZMBEEM00\_0\_6089L.17

14 December 2017

AECOM  
Supervising Officer Representative's Office  
No. 8 Mong Fat Street, Tuen Mun,  
New Territories, Hong Kong

By Fax (2293 6300) and By Post

Attention: Mr. Albert Yu

Dear Mr. Yu,

**Re: Agreement No. CE 48/2011 (EP)  
Environmental Project Office for the  
HZMB Hong Kong Link Road, HZMB Hong Kong Boundary Crossing  
Facilities, and Tuen Mun-Chek Lap Kok Link – Investigation**


**Contract No. HY/2013/12 TM-CLKL Northern Connection Toll Plaza and  
Associated Works  
37<sup>th</sup> Monthly EM&A Report for November 2017 (EP-354/2009/D)**

Reference is made to the Monthly Environmental Monitoring and Audit (EM&A) Report (Nov. 2017) (AUES reference: TCS00715/14/600/R0360v2 dated 13 Dec. 2017) certified by the ET Leader and provided to us via e-mail on 14 Dec. 2017.

Please be informed that we have no adverse comments on the captioned Report. We write to verify the captioned submission in accordance with Condition 4.4 of EP-354/2009/D.

Thank you for your attention. Please do not hesitate to contact the undersigned or the ENPO Leader Mr. Y. H. Hui should you have any queries.

Yours sincerely,



F. C. Tsang  
Independent Environmental Checker  
Tuen Mun – Chek Lap Kok Link

c.c. HyD – Mr. Stephen Chan (By Fax: 3188 6614)  
HyD – Mr. Vico Cheung (By Fax: 3188 6614)  
AECOM – Mr. Conrad Ng (By Fax: 3922 9797)  
AUES – Mr. T. W. Tam (By Fax: 2959 6079)  
CRBC – Kaden JV – Mr. John Wong (By Fax: 2253 8399)

Internal: DY, YH, ENPO Site

Q:\Projects\HYDHZMBEEM00\02\_Proj\_Mgt\02\_Corr\2017\HYDHZMBEEM00\_0\_6089L.17.docx

**EXECUTIVE SUMMARY**

ES01 This is the 37<sup>th</sup> Monthly EM&A Report presenting the monitoring results and inspection findings for the period from **1 to 30 November 2017** (hereinafter ‘the Reporting Period’).

**SUMMARY OF EM&A ACTIVITIES FOR THE REPORTING PERIOD**

ES02 The EM&A activities conducted in the Reporting Period are summary in below:-

- 24-hours TSP of Air Quality Monitoring –**50 events**
- 1-hour TSP of Air Quality Monitoring – **150 events**
- Cultural Heritage Inspection – **4 events**
- Landfill Gas Monitoring – **26 days**
- Landscape & Visual Monitoring – **4 events**
- Environmental Site Inspection – **4 events**

**BREACH OF ACTION AND LIMIT (A/L) LEVELS**

ES03 In the Reporting Period, 2 Action Level and 1 Limit Level exceedances of 1-hour TSP were recorded at ASR5 & ASR 10 on 2 November 2017; 1 Action Level exceedance of 1-hour TSP was recorded at ASR5 on 11 November 2017; 1 Action Level exceedance of 1-hour TSP was recorded at ASR10 on 29 November 2017 according to the measurement results by the ET of Contract HY/2012/08. Investigation reports for the exceedances on 2 and 11 November 2017 were submitted by the ET and concluded that the exceedances were not project related. The investigation report for the exceedance on 29 November 2017 was prepared by the ET and pending for the IEC review. It will be submitted to all relevant parties and included in the next monthly EM&A Report. The summary of breach of air quality performance is shown below.

Environmental Aspect	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	4	1	3	3	0
	24-hour TSP	0	0	0	0	0

ES04 In last Reporting Period, the exceedances of 1-hour and 24-hour TSP were recorded on 21 and 27 October 2017. The investigation reports (IR) were submitted by ET.

ES05 No noise complaints were received in the Reporting Period.

ES06 Landfill gas monitoring was conducted at the TD1 works area in this reporting month by the Safety Officer. The monitoring results shown no exceedances were triggered.

ES07 Site inspection for landscape and visual was conducted on weekly basis by the Landscape Architect to ensure the compliance with the intended aims of the mitigation measures. Most of the landscape works such as planting was not yet commenced.

**SITE INSPECTION**

ES08 In the Reporting Period, joint site inspection by the RE, ET and the Contractor was carried out on **7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> November 2017** and the IEC has attended the joint site inspection on **28<sup>th</sup> November 2017**. No non-compliance was recorded during the site inspection but **1** observation and **4** reminders were recorded.

ES09 Inspection for Pitcher Plants of ecology and grave of culture heritage were also carried out during the weekly site inspection. It was observed that the transplanted pitcher plants were properly protected. Establishment period for the pitcher plants was completed at the end of September 2016 and the final pitcher plants report was submitted to AFCD on early December 2016. Since then only the integrity of the protection fence was checked to fulfil the EIA requirement.

**ENVIRONMENTAL COMPLAINT**

- ES10 In the Reporting Period, no environmental complaint was received.
- ES11 In the last reporting period (1 to 31 October 2017), there was a complaint regarding light nuisance created by Tuen Mun - Chek Lap Kok Link Project during mid-night. The investigation report (IR) has been submitted by ET and concluded that the complaint was not project related.
- ES12 The statistical summary of environmental complaints is summarized in the following table.

Reporting Period	Environmental Complaint Statistics	
	Frequency	Cumulative
Since the Contract commencement	9	9
November 2017	0	9

**NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS**

- ES13 No environmental summons or successful prosecutions were recorded in the Reporting Period.

**REPORTING CHANGE**

- ES14 No reporting changes were made in the Reporting Period.

**FUTURE KEY ISSUES**

- ES15 During dry season, air quality mitigation measures such as watering of site area for 12 times per day and covering of exposed slopes should be fully implemented to reduce construction dust impact as recommended in the EMIS.
- ES16 Moreover, muddy water or other water pollutants from site surface runoff into the public areas will be key environment issue. Special attention should be paid on the water quality mitigation measures to prevent surface runoff flow to public area.
- ES17 It was reminded that good housekeeping practice should be maintained. Mosquito control measures should be properly implemented to prevent mosquito breeding on site especially after rain.

**TABLE OF CONTENTS**

<b>1</b>	<b>INTRODUCTION</b>	<b>1</b>
1.1	CONTRACT BACKGROUND	1
1.2	REPORT STRUCTURE	1
<b>2</b>	<b>CONTRACT ORGANIZATION AND CONSTRUCTION PROGRESS AND ENVIRONMENTAL SUBMISSIONS</b>	<b>2</b>
2.1	CONTRACT ORGANIZATION	2
2.2	CONSTRUCTION PROGRESS	2
2.3	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	2
<b>3</b>	<b>SUMMARY OF IMPACT MONITORING REQUIREMENTS UNDER THE CONTRACT</b>	<b>3</b>
3.1	GENERAL	3
3.2	AIR QUALITY MONITORING	3
3.3	MONITORING LOCATION	3
3.4	MONITORING FREQUENCY	3
3.5	MONITORING EQUIPMENT	4
3.6	DERIVATION OF ACTION/LIMIT (A/L) LEVELS	5
3.7	OTHER ENVIRONMENTAL ASPECTS	5
3.8	MONITORING SCHEDULE	6
<b>4</b>	<b>AIR QUALITY MONITORING</b>	<b>7</b>
4.1	GENERAL	7
4.2	AIR QUALITY MONITORING RESULTS IN REPORTING PERIOD	7
4.3	ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE	7
4.4	AIR QUALITY EXCEEDANCE INVESTIGATION	7
<b>5</b>	<b>ECOLOGY MONITORING</b>	<b>8</b>
5.1	GENERAL	8
5.2	PITCHER PLANTS INSPECTION	8
<b>6</b>	<b>CULTURAL HERITAGE</b>	<b>9</b>
6.1	GENERAL	9
6.2	GRAVE INSPECTION	9
<b>7</b>	<b>LANDSCAPE AND VISUAL</b>	<b>10</b>
7.1	GENERAL	10
7.2	LANDSCAPE AND VISUAL INSPECTION	10
<b>8</b>	<b>LANDFILL GAS HAZARD MONITORING</b>	<b>11</b>
8.1	GENERAL	11
8.2	LANDFILL GAS MONITORING RESULT	12
<b>9</b>	<b>WASTE MANAGEMENT</b>	<b>13</b>
9.1	GENERAL WASTE MANAGEMENT	13
9.2	RECORDS OF WASTE QUANTITIES	13
<b>10</b>	<b>INSPECTION AND AUDIT</b>	<b>14</b>
10.1	SITE INSPECTION	14
<b>11</b>	<b>ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE</b>	<b>16</b>
11.1	ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION	16
<b>12</b>	<b>IMPLEMENTATION STATUS OF MITIGATION MEASURES</b>	<b>17</b>
12.1	GENERAL REQUIREMENTS	17
12.2	TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH	17
12.3	KEY ENVIRONMENTAL ISSUES FOR THE COMING MONTH	18
<b>13</b>	<b>CONCLUSIONS AND RECOMMENDATIONS</b>	<b>19</b>
13.1	CONCLUSIONS	19
13.2	RECOMMENDATIONS	20

**LIST OF TABLES**

TABLE 2-1	STATUS OF ENVIRONMENTAL LICENSES AND PERMITS OF THE CONTRACT
TABLE 3-1	AIR QUALITY MONITORING STATIONS UNDER THE CONTRACT
TABLE 3-2	ENHANCED TSP MONITORING PLAN – CONSTRUCTION PHASE
TABLE 3-3	ACTION AND LIMIT LEVELS FOR IMPACT AIR QUALITY MONITORING
TABLE 4-1	SUMMARY OF AIR QUALITY MONITORING EXCEEDANCE
TABLE 8-1	LANDFILL GAS MONITORING ZONE
TABLE 8-2	SUMMARY OF LANDFILL GAS MEASUREMENT RESULTS
TABLE 9-1	SUMMARY OF QUANTITIES OF INERT C&D MATERIALS
TABLE 9-2	SUMMARY OF QUANTITIES OF C&D WASTES
TABLE 10-1	SITE OBSERVATIONS FOR THE CONTRACT
TABLE 10-2	OUTSTANDING ITEMS IN SITE INSPECTION OF PREVIOUS REPORTING PERIOD
TABLE 11-1	STATISTICAL SUMMARY OF ENVIRONMENTAL EXCEEDANCE
TABLE 11-2	STATISTICAL SUMMARY OF ENVIRONMENTAL COMPLAINTS
TABLE 11-3	STATISTICAL SUMMARY OF ENVIRONMENTAL SUMMONS
TABLE 11-4	STATISTICAL SUMMARY OF ENVIRONMENTAL PROSECUTION
TABLE 12-1	ENVIRONMENTAL MITIGATION MEASURES

**LIST OF APPENDICES**

APPENDIX A	PROJECT LAYOUT PLAN
APPENDIX B	LAYOUT PLAN OF THE CONTRACT
APPENDIX C	ORGANIZATION OF THE CONTRACT
APPENDIX D	THREE MONTHS ROLLING PROGRAMME
APPENDIX E	MONITORING LOCATIONS FOR THE CONTRACT
APPENDIX F	EVENT AND ACTION PLAN
APPENDIX G	MONITORING SCHEDULE
APPENDIX H	CALIBRATION CERTIFICATES OF MONITORING EQUIPMENT
APPENDIX I	LANDFILL GAS MONITORING RESULTS AND GRAPHICAL PLOTS
APPENDIX J	INVESTIGATION REPORT FOR EXCEEDANCE
APPENDIX K	CHECKLIST FOR LANDSCAPE AND VISUAL MONITORING
APPENDIX L	MONTHLY SUMMARY WASTE FLOW TABLE
APPENDIX M	ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURES IMPLEMENTATION SCHEDULE (EMIS)
APPENDIX N	CUMULATIVE STATISTICS ON EXCEEDANCE AND COMPLAINT
APPENDIX O	INVESTIGATION REPORT FOR THE COMPLAINT
APPENDIX P	INSPECTION CHECKLIST FOR VULNERABLE TO CONTAMINATED WATER DISCHARGE

## 1 INTRODUCTION

### 1.1 CONTRACT BACKGROUND

1.1.1 CRBC-Kaden Joint Venture (hereafter “CRBC-Kaden JV”) is commissioned by the Highways Department (HyD) as the Main Contractor of the Contract No. HY/2013/12 – Northern Connection Toll Plaza and Tunnel Section ((hereafter “the Contract”) and this Contract is part of the Tuen Mun – Chek Lap Kok Link (TM-CLK Link Project). TM-CLK Link Project is a Designated Project under Environmental Permit number EP-354/2009/D issued on 13 March 2015. The layout Plan of the Project and the Contract are showed in [Appendix A](#) and [B](#) respectively.

1.1.2 The construction works of the Contract mainly include:-

- a. construction of an approximately 5.4 hectares toll plaza and an associated footbridge;
- b. construction of associated carriageways including approximately 0.74 kilometre land viaducts, and an approximately 230 metres vehicular underpass to connect the toll plaza and the roundabout at Lung Mun Road/Lung Fu Road;
- c. site formation for the construction of the toll plaza, including associated slope works and natural terrain hazard mitigation measures;
- d. modification and realignment of the existing Lung Mun Road and Lung Fu Road; and
- e. associated waterworks, drainage, sewerage and landscaping works, etc..

1.1.3 This is 37<sup>th</sup> monthly EM&A report presenting the monitoring results and inspection findings for period from **1 to 30 November 2017**.

### 1.2 REPORT STRUCTURE

1.2.1 The Monthly Environmental Monitoring and Audit (EM&A) Report is structured into the following sections:-

*Section 1 Introduction*

*Section 2 Contract Organization and Construction Progress and Environmental Submissions*

*Section 3 Summary of Impact Monitoring Requirements under the Contract*

*Section 4 Air Quality Monitoring*

*Section 5 Ecology Monitoring*

*Section 6 Cultural Heritage*

*Section 7 Landscape and Visual*

*Section 8 Landfill gas hazard Monitoring*

*Section 9 Waste Management*

*Section 10 Inspections and Audit*

*Section 11 Environmental Complaints and Non-Compliance*

*Section 12 Implementation Status of Mitigation Measures*

*Section 13 Conclusions and Recommendations*

## 2 CONTRACT ORGANIZATION AND CONSTRUCTION PROGRESS AND ENVIRONMENTAL SUBMISSIONS

### 2.1 CONTRACT ORGANIZATION

2.1.1 The Contract organization and contact details of key personnel are shown in [Appendix C](#).

### 2.2 CONSTRUCTION PROGRESS

2.2.1 In the Reporting Period, the major construction activity conducted under the Contract is summarized in below. The three-months rolling programme of the Contract is enclosed in [Appendix D](#).

- Instrumentation and Monitoring
- Site Formation – Earthwork on Slope D and E; surface drainage on Slope C, D & E and Portion H;
- Toll Plaza Decking TD1 and TD2;
- Toll Plaza Footbridge;
- Retaining Structure RW\_A, RW\_B
- Toll Collector Subway & Associated Works;
- Bridge G1 and H1 by Form Traveller;
- Sewer Culvert at FC1 and FC2;
- Road and Drainage Works at +11mPD, +19mPD and Portion H.
- Toll Booth Canopy
- Road pavement works at +19mPD platform ;
- Construction of bus shelter

### 2.3 SUMMARY OF ENVIRONMENTAL SUBMISSIONS

2.3.1 The environmental submissions under the EP requirement had been submitted to the EPD and they are listed in below:

- Monitoring Plan on Construction Dust (submission refer to Contract HY/2012/08)
- Landscape and Visual Plan (not yet endorsed by EPD)
- Waste Management Plan (endorsed by EPD on 16 March 2015)
- Baseline Monitoring Report (not yet endorsed by EPD)

2.3.2 Summary of environmental permits, licenses and notifications for the Contract is presented in [Table 2-1](#).

**Table 2-1 Status of Environmental Licenses and Permits of the Contract**

No.	Type of Permit/ License	Reference/ License No.	Date of Issue	Date of Expiry
1	Air pollution Control (Construction Dust) Regulation	377719	06-08-2014	N/A
2	Chemical Waste Producer Registration - Waste Producers Number	5117422C389301	03-09-2014	N/A
3	Water Pollution Control Ordinance -Variation of Effluent Discharge License	WT00023973-2016	14-03-16	30-09-2019
4	Water Pollution Control Ordinance – New Variation of Effluent Discharge License	WT00023973-2016	18-05-2016	30-09-2019
5	Waste Disposal Regulation - Billing Account for Disposal of Construction Waste	7020460	01-08-2014	N/A
6	Extend CNP for Flasework Erection	GW-RW0563-17	26-10-2017	24-02-2018
7	Extend CNP for Multiple Task	GW-RW0605-17	25-11-2017	24-05-2018
8	Extent CNP for Tunnel Works	GW-RW0567-17	26-10-2017	22-05-2018
9	CNP for Portion H	GW-RW0568-17	26-10-2017	22-05-2018
10	CNP for Road Paving Works	GW-RW0561-17	26-10-2017	01-02-2018



### 3 SUMMARY OF IMPACT MONITORING REQUIREMENTS UNDER THE CONTRACT

#### 3.1 GENERAL

3.1.1 The major construction activities under the Contract are land-based and no marine work will be involved. In accordance with the Project EM&A Manual requirements, the environmental aspects under the Contract shall be included air quality, ecological, cultural heritage, landscape and visual, landfill gas and site inspection during construction period. In addition, audit of the contractor's implementation of the construction noise and land-based water quality pollution control measures are also required for the Contract.

3.1.2 A summary of construction phase EM&A requirements are presented in the sub-sections below.

#### 3.2 AIR QUALITY MONITORING

3.2.1 The construction phase air quality monitoring shall cover the following parameters:

- 1-hour TSP; and
- 24-hour TSP

#### 3.3 MONITORING LOCATION

3.3.1 The air quality monitoring stations for impact monitoring are listed in [Table 3-1](#) and illustrated in [Appendix E](#).

**Table 3-1 Air Quality Monitoring Stations under the Contract**

ID	Location	Air monitoring station Description
ASR1	Tuen Mun Fireboat Station	EM&A Manual
ASR5	Pillar Point Fire Station	EM&A Manual
AQMS1	Previous River Trade Golf	Enhanced TSP Level under EP condition 2.4
ASR6	Butterfly Beach Laundry	Enhanced TSP Level under EP condition 2.4
ASR10	Butterfly Beach Park	Enhanced TSP Level under EP condition 2.4

#### 3.4 MONITORING FREQUENCY

3.4.1 As per Condition 2.4 of the EP of TM-CLKL, an enhanced monitoring plan on TSP level at Tuen Mun ("the Enhanced TSP Monitoring Plan") is required to be submitted to the DEP for approval at least 1 month before the commencement of construction of the Project. Details of the Enhanced TSP Monitoring Plan under Contract No. HY/2012/08 could be found from the project website. The air quality monitoring work under this Contract will follow the monitoring requirement of enhanced TSP monitoring under the project.

3.4.2 The air quality monitoring requirements for the Contract is summarized in [Table 3-2](#).

**Table 3-2 Enhanced TSP Monitoring Plan – Construction Phase**

Condition	Monitoring Parameter	Monitoring Location	Frequency	Monitoring Requirement
General	1-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10	3 times per day every six days	Throughout the Northern Connection, toll plaza and tunnel buildings construction works
	24-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10	Daily every six days	
Special	1-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10	3 times per day every three days	<b><u>Northern Connection</u></b> During excavation works for launching shaft, excavation work for Cut and Cover Tunnel and Cut and Cover Tunnel Construction <b><u>Toll Plaza</u></b>
	24-hour TSP	ASR1, ASR5, AQMS1, ASR6, ASR10	Daily every three days	

Condition	Monitoring Parameter	Monitoring Location	Frequency	Monitoring Requirement
				During excavation, slope works, construction of road and superstructures and wind erosion from open sites and stockpiling areas <u><b>Tunnel Buildings</b></u> During excavation, foundation works, construction of superstructures and wind erosion from open sites and stockpiling areas

### 3.5 MONITORING EQUIPMENT

- 3.5.1 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*.
- 3.5.2 A high volume sampler in compliance with the following specifications shall be used for carrying out the 1-hr and 24-hr TSP monitoring:
- (i) 0.6-1.7 m<sup>3</sup>/min (20-60 SCFM) adjustable flow range;
  - (ii) equipped with a timing/control device with +/- 5 minutes accuracy for 24 hours operation;
  - (iii) installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
  - (iv) capable of providing a minimum exposed area of 406 cm<sup>2</sup> (63 in<sup>2</sup>);
  - (v) flow control accuracy: +/- 2.5% deviation over 24-hr sampling period;
  - (vi) equipped with a shelter to protect the filter and sampler;
  - (vii) incorporated with an electronic mass flow rate controller or other equivalent devices;
  - (viii) equipped with a flow recorder for continuous monitoring;
  - (ix) provided with a peaked roof inlet;
  - (x) equipped with a manometer;
  - (xi) able to hold and seal the filter paper to the sampler housing in a horizontal position;
  - (xii) easy to change the filter; and
  - (xiii) capable of operating continuously for 24-hr period.
- 3.5.3 Calibration of dust monitoring equipment shall be conducted by the ET upon installation and in bi-monthly intervals during construction phase. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The calibration data shall be properly documented for future reference by concerned parties, such as the IEC. All the data shall be converted into standard temperature and pressure condition.
- 3.5.4 The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.
- 3.5.5 If the ET Leader proposes to use a direct reading dust meter to measure 1-hr TSP levels on an ad hoc basis, he shall submit sufficient information to the IEC to prove that the instrument is capable of achieving a comparable result as that the High Volume Sampler (HVS) and may be used for the 1-hr sampling. The instrument should also be calibrated regularly and the 1-hr sampling shall be checked periodically by the HVS to check the validity and accuracy of the results measured by the direct reading method.
- 3.5.6 According to the Project EM&A Manual, wind data monitoring equipment shall also be provided and set up for logging wind speed and wind direction near the dust monitoring locations. The equipment installation location shall be proposed by the ET Leader and

agreed with the IEC. For installation and operation of wind data monitoring equipment, the following points shall be observed:

- (i) the wind sensors should be installed on masts at an elevated level 10 m above ground so that they are clear of obstructions or turbulence caused by the buildings;
- (ii) the wind data should be captured by a data logger to be down-loaded for processing at least once a month;
- (iii) the wind data monitoring equipment should be re-calibrated at least once every six months; and
- (iv) wind direction should be divided into 16 sectors of 22.5 degrees each.

### 3.6 DERIVATION OF ACTION/LIMIT (A/L) LEVELS

3.6.1 The baseline monitoring results formed the basis for determining the air quality criteria for the impact monitoring. The ET shall compare the impact monitoring results with air quality criteria set up for 24-hour TSP and 1-hour TSP. Based on results of the approved Baseline Monitoring Report of HyD Contract HY/2012/08, the Action and Limit Levels for impact dust monitoring are shown in [Tables 3-3](#).

**Table 3-3 Action and Limit Levels for Impact Air Quality Monitoring**

Air Quality Monitoring Stations	24-hour TSP ( $\mu\text{g}/\text{m}^3$ )		1-hour TSP ( $\mu\text{g}/\text{m}^3$ )	
	Action Level	Limit Level	Action Level	Limit Level
ASR1	213	260	331	500
ASR5	238	260	340	500
AQMS1	213	260	335	500
ASR6	238	260	338	500
ASR10	214	260	337	500

3.6.2 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan which presented in [Appendix F](#).

### 3.7 OTHER ENVIRONMENTAL ASPECTS

#### Noise

3.7.1 The TM-CLKL EIA study stated that no existing noise sensitive receiver (NSR) was identified within the Study Area at Tuen Mun. Therefore, no noise monitoring is required for the construction phase of the Contract.

3.7.2 Regular site inspections and audits will be carried out during the construction phase in order to confirm the construction works under the Contract comply with the regulatory noise requirements.

#### Water Quality

3.7.3 No marine works will be undertaken under the Contract. Therefore, no water quality monitoring is required for the construction phase of the Contract.

#### Ecology

3.7.4 No marine works will be undertaken under the Contract and generated marine ecological impact, no dolphin monitoring is required for the construction phase of the Contract.

3.7.5 During construction phase, the ET will perform Pitcher Plants inspection at least once every week to report the growth condition (only undertaken at Establishment period) and protection measures.

#### Landscape and Visual

3.7.6 Measures to mitigate landscape and visual impact during construction should be checked and monitored by a Registered Landscape Architect to ensure compliance with the intended aims

of the mitigation measures in accordance with the EM&A Manual.

**Cultural Heritage**

- 3.7.7 Grave G1 as a heritage resource is situated near the proposed toll plaza in Tuen Mun. Site inspections should be undertaken at least once per week throughout the construction period to ensure compliance with the intended aims of recommended mitigation measures.

**Landfill Gas**

- 3.7.8 During EIA study, landfill gas hazards are likely to be generated from the Pillar Point Valley (PPV) Landfill. Landfill gas monitoring is recommended during construction of the Contract to ensure the works area is free of landfill gas before the worker entered the concerned area.

**3.8 MONITORING SCHEDULE**

- 3.8.1 The monitoring schedule for landscape & visual and landfill gas for the present and next reporting period are presented in [Appendix G](#).

## 4 AIR QUALITY MONITORING

### 4.1 GENERAL

4.1.1 The air quality impact monitoring and enhanced Total Suspended Particulates (TSP) level monitoring at five proposed locations are currently carried out by the ET of Contract HY/2012/08. Sharing of impact air quality monitoring data between HY/2012/08 and HY/2013/12 is agreed by all relevant parties. The Contract is not required to conduct its own dust monitoring exercise until the Contract HY/2012/08 ends.

### 4.2 AIR QUALITY MONITORING RESULTS IN REPORTING PERIOD

4.2.1 In the Reporting Period, 1-hour and 24-hour TSP monitoring at the five proposed locations are continued to perform by the ET of Contract HY/2012/08. Therefore, no air quality monitoring was conducted by the ET of Contract HY/2013/12. Details information of air quality monitoring results could be referred to the Monthly EM&A Reports of the Contract HY /2012 /08 ([November 2017](#)).

### 4.3 ACTION AND LIMIT (A/L) LEVELS EXCEEDANCE

4.3.1 According to the air quality monitoring result provided by Contract HY/2012/08, 2 Action Level and 1 Limit Level exceedances of 1-hour TSP were recorded at ASR5 & ASR 10 on 2 November 2017; 1 Action Level exceedance of 1-hour TSP was recorded at ASR5 on 11 November 2017; 1 Action Level exceedance of 1-hour TSP was recorded at ASR10 on 29 November 2017. The summary of air quality exceedance in the Reporting Period is shown in [Table 4-1](#).

**Table 4-1 Summary of Air Quality Monitoring Exceedance**

Date of Exceedance	Monitoring Station	Air Quality Parameter	Result	Exceed
2 November 2017	ASR5	1Hr TSP	351 $\mu\text{g}/\text{m}^3$	Action Level
2 November 2017	ASR10	1Hr TSP	403 $\mu\text{g}/\text{m}^3$	Action Level
2 November 2017	ASR10	1Hr TSP	816 $\mu\text{g}/\text{m}^3$	Limit Level
11 November 2017	ASR5	1Hr TSP	389 $\mu\text{g}/\text{m}^3$	Action Level
29 November 2017	ASR10	1Hr TSP	455 $\mu\text{g}/\text{m}^3$	Action Level

### 4.4 AIR QUALITY EXCEEDANCE INVESTIGATION

4.4.1 Investigation reports for the exceedances on 2 and 11 November 2017 were submitted by the ET and concluded that the exceedances were not project related and the IRs of the exceedance conducted by the ET is shown in [Appendix J](#). The investigation report for the exceedance on 29 November 2017 was prepared by the ET and pending for the IEC review. The IR of the exceedances would be presented in the next Monthly EM&A Report (December 2017).

4.4.2 In last Reporting Period, the investigation reports (IR) of the exceedance of 1-hour and 24-hour TSP on 21 and 27 October 2017 were submitted by ET. After the investigation, it is concluded that the exceedance were not project related. The IR of the exceedance conducted by the ET is shown in [Appendix J](#).

## **5 ECOLOGY MONITORING**

### **5.1 GENERAL**

5.1.1 According to the EM&A Manual requirements, regularly inspection for Pitcher Plants shall be conducted at least once every week to report the protection measure of the Pitcher Plants during construction period.

5.1.2 A total of 181 pitcher plants were transplanted to final receptor site and the rest of the Pitcher Plant individuals (certified dead by the specialist) were not transplanted and were treated as general refuse. All the transplantation of pitcher plant from the nursery site to final receptor site was completed on 10<sup>th</sup> September 2015.

### **5.2 PITCHER PLANTS INSPECTION**

5.2.1 Inspection for the mitigation measures implementation status of the Pitcher Plant at the final receptor area were performed on **7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> November 2017** by the ET in the Reporting Period.

5.2.2 Establishment period for the pitcher plants was completed at the end of September 2016, the joint site completion of Establishment period visit with AFCD was undertaken on 23 September 2016 and the final pitcher plants report was submitted to AFCD on early December 2016. Therefore after 23 September 2016, only the integrity of the protection fence was checked to fulfil the EIA requirement. During each inspection, the protection mitigation measures were checking at the final receptor area to make sure no site activities was undertaken inside the protection zone. Besides, no construction activities were observed to be carried out at the surrounding of the final receptor area. The condition of chain link fence is good and no repair or maintenance is required.

5.2.3 No matters the completion of Establishment period, the Contractor should properly maintain the fencing along the receptor area to avoid disturbance to the pitcher plants under the EIA requirement.

## 6 CULTURAL HERITAGE

### 6.1 GENERAL

6.1.1 According to the EM&A Manual requirements, regular inspection for heritage resource, Grave G1, shall be audited by the ET at least once every week to ensure recommended mitigation measures implemented during construction period. The aim of the survey is to prevent any possible damage to the grave and to ensure the proposed mitigation measures are implemented. The broad scope of the audit will involve supervision of the following:

- Non-contact effects of the engineering works, such as vibration from pneumatic drills which could cause damage, such as foundation or wall cracks and loosening of tiles or fixtures; and
- Contact between the historic structures and equipment and materials associated with the engineering works.

6.1.2 Specifically, the monitoring programme will entail the following tasks:

- The extent of the agreed works areas should be regularly checked during the construction phase to ensure the buffer is being maintained; and
- Ensure no stockpiling or equipment storage is affecting the structure.

6.1.3 In the event of non-compliance the responsibilities of the relevant parties is detailed in the Event/ Action Plan in *Appendix F*.

### 6.2 GRAVE INSPECTION

6.2.1 In the Reporting Period, Grave G1 of inspection was undertaken on **7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> November 2017**. During these inspections, buffer zone was maintained between the working area and the Grave. The nearby areas were clean, and no construction materials or mechanical equipment were stored within or close to the buffer zone. Moreover protective measures (hoarding and scaffold with protective net above the grave) was provided for constructing Toll Plaza Decking TD2 deck structure.

6.2.2 Since construction works very close to buffer zone of the Grave G1, cultural heritage mitigation measures and protection measures as provided by the Contractor, therefore has fully implemented in accordance with EM&A Manual requirements.

## 7 LANDSCAPE AND VISUAL

### 7.1 GENERAL

7.1.1 According to EM&A Manual requirements, monitoring of Contractor's operations during construction period to report on Contractor's compliance should be carried out on weekly basis. Measure to mitigate landscape and visual impact during construction should be checked and monitored by a Registered Landscape Architect to ensure compliance with the intended aims of the mitigation measures. Moreover, the progress of the engineering works shall be regularly reviewed on site to identify the earliest practical opportunities for the landscape works to be undertaken.

### 7.2 LANDSCAPE AND VISUAL INSPECTION

7.2.1 In the Reporting Period, site inspection for landscape and visual mitigation measures was undertaken on **3<sup>rd</sup>, 10<sup>th</sup>, 17<sup>th</sup> and 24<sup>th</sup> November 2017** by the Registered Landscape Architect.

7.2.2 Most of the landscape works such as planting was not yet commenced, but some transplanting works was commenced on 22 May 2017. The detailed inspection checklists were provided in ***Appendix K***.



## 8 LANDFILL GAS HAZARD MONITORING

### 8.1 GENERAL

- 8.1.1 During EIA study, landfill gas hazards are likely to be generated from the Pillar Point Valley (PPV) Landfill. Hence, regular landfill gas monitoring is recommended during construction of the proposed toll plaza.
- 8.1.2 During construction, a Safety Officer should be appointed to carry out the monitoring works. The monitoring frequency and areas to be monitored should be set down prior to commencement of ground-works either by the Safety Officer or an approved and appropriated qualified person. The routine monitoring should be carried out in all excavations, manholes, chambers, relocation of monitoring wells and any other confined spaces that may have been created. All measurements in excavations should be made with the extended monitoring tube located not more than 10 mm from the exposed ground surface. Monitoring should be performed properly to make sure that the area is free of landfill gas before any man enters in the area.
- 8.1.3 For excavations deeper than 1m, measurements should be carried out:
- at the ground surface before excavation commences;
  - immediately before any worker enters the excavation;
  - at the beginning of each working day for the entire period the excavation remains open; and
  - periodically through the working day whilst workers are in the excavation.
- 8.1.4 For excavations between 300mm and 1m deep, measurements should be carried out:
- directly after the excavation has been completed; and
  - periodically whilst the excavation remains open
- 8.1.5 For excavations less than 300mm deep, monitoring may be omitted, at the discretion of the Safety Officer (SO) or other appropriately qualified person.
- 8.1.6 To ensure the accuracy of the monitoring data, zeroing of the gas analyser shall be undertaken at the start of each day's monitoring. As advised by the SO, the gas analyser would be optimally calibrated by the self-test function to provide the most accurate result. The gas analyser is calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.
- 8.1.7 The landfill consultation zone was divided into 6 monitoring zones. The landfill gas monitoring zones are summarized in [Table 8-1](#) and the layout plan for the monitoring zone is illustrated in [Appendix E](#).

**Table 8-1 Landfill Gas Monitoring Zone**

ID	Location	Excavation >300mm deep undertaken in this reporting period
TD1	TD1, Retaining Wall A, Grave G1 and Subway	Yes
RW-B	Retaining Wall B	No
RW-F	Retaining Wall F	No
S&U	Slope and Underpass	No
BW	Bridge Works (G2, H1)	No
LMR	Lung Mun Road	No

**8.2 LANDFILL GAS MONITORING RESULT**

8.2.1 In the Reporting Period, landfill gas monitoring was conducted at the zone TD1 which have excavation works was undertaking. A BIOGAS 5000 gas analyser was used for the landfill gas monitoring and the valid calibration certificate is presented in [Appendix H](#).

8.2.2 There were a total of **26** days monitoring were carried by the Safety Officer or an approved and qualified persons. The results of landfill gas measurement are summarized in [Table 8-2](#). Moreover, database of monitoring result and graphical plot are attached in [Appendix I](#).

**Table 8-2 Summary of Landfill Gas Measurement Results**

Landfill Gas Parameter	Action Level	Limit Level	Detectable at TD1	
			Min	Max
<b>Methane</b>	>10% LEL (>0.5% v/v)	>20% LEL (>1% v/v)	0.1%	0.1%
<b>Oxygen</b>	<19%	<18%	20.7%	21.1%
<b>Carbon Dioxide</b>	>0.5%	>1.5%	0.1%	0.2%

8.2.3 The measurement results shown that slightly methane concentration was detected and oxygen concentration measured was over 19.0 % and Carbon Dioxide was between 0.1% and 0.2 %. No exceedance was triggered and therefore no corrective action was required accordingly.

## 9 WASTE MANAGEMENT

### 9.1 GENERAL WASTE MANAGEMENT

9.1.1 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time. The effective management of waste arising during the construction phase will be monitored through the site audit programme. The aims of the waste audit are:

- to ensure the waste arising from the works are handled, stored, collected, transferred and disposed of in an environmentally acceptable manner; and
- to encourage the reuse and recycling of material.

9.1.2 In addition to the site inspections, the ET shall review the documentation procedures prepared by the Waste Coordinator once a week to ensure proper records are being maintained and procedures undertaken in accordance with the Waste Management Plan.

### 9.2 RECORDS OF WASTE QUANTITIES

9.2.1 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil.

9.2.2 The quantities of wastes generated under the Contract in this Reporting Period are summarized in [Tables 9-1](#) and [9-2](#) and the Monthly Summary Waste Flow Table is shown in [Appendix L](#). Whenever possible, materials were reused on-site as far as practicable.

**Table 9-1 Summary of Quantities of Inert C&D Materials**

Type of Waste	Quantity	Disposal Location
Reused in this Contract (Inert) ( $\times 1000\text{m}^3$ )	0.871	-
Reused in other Projects (Inert) ( $\times 1000\text{m}^3$ )	26.510	1. Lam Tei Quarry 2. Eco Park K.Wah Recycle Facilities 3. Lung Kwu Tan Tailor Recycled Aggregates 4. Liantang BCP Project 5. TM-CLKL Contract 2 - Northern Connection Sub-sea Tunnel Section Project
Disposal as Public Fill (Inert) ( $\times 1000\text{m}^3$ )	1.557	Tuen Mun Area 38

**Table 9-2 Summary of Quantities of C&D Wastes**

Type of Waste	Quantity	Disposal Location
Recycled Metal ( $\times 1000\text{kg}$ )	0	-
Recycled Paper / Cardboard Packaging ( $\times 1000\text{kg}$ )	0	-
Recycled Plastic ( $\times 1000\text{kg}$ )	0	-
Chemical Wastes ( $\times 1000\text{kg}$ )	0	License Collector
General Refuses ( $\times 1000\text{m}^3$ )	0.880	WENT

## 10 INSPECTION AND AUDIT

### 10.1 SITE INSPECTION

10.1.1 According to the approved EM&A Manual, the environmental site inspection shall be formulated by ET Leader on weekly basis to confirm the environmental performance of the construction site.

#### *Findings / Deficiencies During Reporting Period*

10.1.2 In the Reporting Period, joint site inspections to evaluate site environmental performance were carried out by the RE, ET and the Contractor on **7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> November 2017**. No non-compliance was noted but **1** observation and **4** reminders were recorded during site inspection. Moreover, ENPO/IEC has attended joint site inspection on **28<sup>th</sup> November 2017**.

10.1.3 The findings / deficiencies observed during the weekly site inspection in the Reporting Period are listed in **Table 10-1**.

**Table 10-1 Site Observations for the Contract**

Date	Findings / Deficiencies	Follow-Up Status
7 November 2017	<ul style="list-style-type: none"> <li>Nil</li> </ul>	<ul style="list-style-type: none"> <li>NA</li> </ul>
14 November 2017	<ul style="list-style-type: none"> <li>Stagnant water cumulated inside the precasted gully was observed. Stagnant water inside the gully should be cleaned to prevent mosquito breeding. (Portion J)</li> </ul>	<ul style="list-style-type: none"> <li>Stagnant water cumulated inside the precasted gully was cleared.</li> </ul>
	<ul style="list-style-type: none"> <li>Temporary drainage should be installed at the new works area. (Portion F)</li> </ul>	<ul style="list-style-type: none"> <li>Not required for reminder.</li> </ul>
	<ul style="list-style-type: none"> <li>Construction materials should not be stored inside the retaining tree protection area. (Portion J)</li> </ul>	<ul style="list-style-type: none"> <li>Not required for reminder.</li> </ul>
21 November 2017	<ul style="list-style-type: none"> <li>Water spraying frequency should be increased for the haul road and exposed area to minimize dust generation. (General)</li> </ul>	<ul style="list-style-type: none"> <li>Not required for reminder.</li> </ul>
	<ul style="list-style-type: none"> <li>Earth bund or mitigation measures should be provided for the inlet of the outfall 1 to prevent muddy water overflow into the outlet. (Butterfly Beach)</li> </ul>	<ul style="list-style-type: none"> <li>Not required for reminder.</li> </ul>
28 November 2017	<ul style="list-style-type: none"> <li>Nil</li> </ul>	<ul style="list-style-type: none"> <li>NA</li> </ul>

10.1.4 No outstanding deficiency remained to be rectified in previous Reporting Period which presented in **Table 10-2**.

**Table 10-2 Outstanding Items in Site Inspection of previous Reporting Period**

Date	Findings / Deficiencies	Follow-Up Status
--	<ul style="list-style-type: none"> <li>NA</li> </ul>	<ul style="list-style-type: none"> <li>NA</li> </ul>

10.1.5 Air quality mitigation measures such as watering of site area for 12 times per day and covering of exposed slopes should be implemented during the construction period to reduce

construction dust impact as recommended in the EMIS.

- 10.1.6 Good site practice for daily housekeeping is reminded. In addition, clean-up of the waste skips and wastewater treatment system should be increased to ensure these facilities functional and effective.
- 10.1.7 In addition, muddy water or other water pollutants from site surface runoff shall not be discharged into public areas. Water quality mitigation measures to prevent surface runoff into the public areas should be paid on special attention.
- 10.1.8 Stagnant water should be removed as soon as possible after rain to prevent mosquito breeding on site.

*Inspection Checklist for Vulnerable to Contaminated Water Discharge*

- 10.1.9 Following to the complaint about discharge of milky water to Bufferfuly Beach on 2 September 2015. The Contractor proposed to carry out daily inspection of wastewater treatment facilities, concerned discharge points, drainage inlets and outlets during typhoon or wet season.
- 10.1.10 In addition, specific inspections would also be conducted before and after adverse weather to ensure necessary remedial works would be carried out timely. Should incidental contaminated water discharge be found at the inlet of the associated drainage system, a specific inspection of the relevant drainage pipes would be conducted for traces of deposit, and follow up actions would be taken when necessary.
- 10.1.11 During the dry season, the frequency of inspection for vulnerable to contaminated water discharge was reduced to once per week by the Contractor at **November 2017**. As requested by the EPD, the associated inspection checklist should be presented in the Monthly EM&A Report and it is shown in *Appendix P*.

## 11 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

### 11.1 ENVIRONMENTAL COMPLAINT, SUMMONS AND PROSECUTION

11.1.1 In the Reporting Period, no environmental complaint, summons and prosecution under the EM&A Programme was lodged. However five exceedance of the environmental performance limit (4 Action Level and 1 Limit Level) were recorded for monitoring programme. Follow up actions have been undertaken by the Contractor to resolve the deficiencies.

11.1.2 In last Reporting Period, the complaint regarding light nuisance created by Tuen Mun - Chek Lap Kok Link Project during mid-night. The investigation was completed and concluded that the complaint was not project related. The IR of the complaint is shown in [Appendix O](#).

11.1.3 The statistical summary table of environmental exceedance, complaint, summons and prosecution are presented in [Tables 11-1, 11-2, 11-3 and 11-4](#).

**Table 11-1 Statistical Summary of Environmental Exceedance**

Reporting Period	Environmental Aspect / Parameter	Environmental Performance	Event Exceedance		
			Reporting Month	Previous Months	Cumulative
November 2017	Air Quality - 1-hr TSP	Action Level	4	18	22
		Limit Level	1	1	2
	Air Quality - 24-hr TSP	Action Level	0	0	1
		Limit Level	0	0	0

**Table 11-2 Statistical Summary of Environmental Complaints**

Reporting Period	Environmental Complaint Statistics					
	Frequency	Cumulative	Complaint Nature			
			Air	Noise	Water	Others
November 2017	0	9	2	NA	6	1

**Table 11-3 Statistical Summary of Environmental Summons**

Reporting Period	Environmental Summons Statistics				
	Frequency	Cumulative	Complaint Nature		
			Air	Noise	Water
November 2017	0	0	NA	NA	NA

**Table 11-4 Statistical Summary of Environmental Prosecution**

Reporting Period	Environmental Prosecution Statistics				
	Frequency	Cumulative	Complaint Nature		
			Air	Noise	Water
November 2017	0	0	NA	NA	NA

11.1.4 In the Reporting Period, no warning letter related to environmental issue was received from the EPD or HyD.

## 12 IMPLEMENTATION STATUS OF MITIGATION MEASURES

### 12.1 GENERAL REQUIREMENTS

- 12.1.1 The environmental mitigation measures that recommended in the Environmental Mitigation and Enhancement Measures Implementation Schedule (EMIS) for in the Project EM&A Manual covered the issues of air quality, cultural heritage, ecology, landfill gas hazard, landscape & visual, noise, water and waste. The updated EMIS for the Contract is shown in [Appendix M](#).
- 12.1.2 The Contractor shall implement the required environmental mitigation measures according to the EM&A Manual as subject to the site condition. The environmental mitigation measures implemented by the Contract in this Reporting Period are summarized in [Table 12-1](#) and [Appendix M](#).

**Table 12-1 Environmental Mitigation Measures**

Issues	Environmental Mitigation Measures
Air Quality	<ul style="list-style-type: none"> <li>• Maintain damp / wet surface on access road</li> <li>• Keep slow speed in the sites</li> <li>• All vehicles must use wheel washing facility before off site</li> <li>• Sprayed water during rock breaking works</li> <li>• During transportation by truck, materials loaded lower than the side and tail boards, and covered before transport</li> <li>• Compacted all soil stockpiles</li> <li>• Part of the exposed slopes covered geotextile net</li> </ul>
Cultural Heritage	<ul style="list-style-type: none"> <li>• Set a buffer zone between the working area and the Grave</li> <li>• All construction materials and equipment store far from the Grave</li> <li>• Inspection the Grave to ensure provision mitigation measures effective</li> </ul>
Ecology	<ul style="list-style-type: none"> <li>• Wire fencing provided for temporary protect Pitcher Plants</li> <li>• Undertake weekly inspection of Pitcher Plants</li> </ul>
Landfill Gas Hazard	<ul style="list-style-type: none"> <li>• Landfill Gas measurement undertake during trench excavation</li> </ul>
Water Quality	<ul style="list-style-type: none"> <li>• Temporary drainage system provide for surface runoff prevent discharge to public area</li> <li>• Wastewater to be treated by sedimentation tank before discharge.</li> </ul>
Noise	<ul style="list-style-type: none"> <li>• No operation of powered mechanical equipment is allowed during restricted hours from 19:00 to 07:00 on the following day and whole day during Sunday and public holiday without construction noise permit (CNP)</li> <li>• Keep good maintenance of plants</li> <li>• The noisy plants or works provide mobile noise barriers</li> <li>• Shut down the plants when not in use</li> </ul>
Waste and Chemical Management	<ul style="list-style-type: none"> <li>• On-site sorting prior to disposal</li> <li>• Follow requirements and procedures of the “Trip-ticket System”</li> <li>• Predict required quantity of concrete accurately</li> <li>• Collect the unused fresh concrete at designated locations in the sites for subsequent disposal</li> </ul>
General	<ul style="list-style-type: none"> <li>• The site was generally kept tidy and clean.</li> </ul>

### 12.2 TENTATIVE CONSTRUCTION ACTIVITIES IN THE COMING MONTH

- 12.2.1 Construction activities as undertaken in the coming month for the Contract lists below:
- Site Formation – Earthwork at 5SE-D/C170; surface drainage on Slope C, D & E and Portion H;
  - Parapet construction for Retaining Structure RW\_A and Bridge G2;
  - Temporary Traffic Arrangement at Lung Mun Road and Lung Fu Road;
  - Toll Collector Subway & Associated Works;
  - Toll booth canopy
  - Road pavement works at +19mPD platform ;
  - Construction of bus shelter

- Bridge G1C and H1C by Formtraveller at Portion F;
- Bridge G1b at Portion F;
- Piling at Portion F ;
- Vehicular Underpass cable trough construction;
- Retaining Structure TP\_G at Portion H;
- Installation of PMMA panel at footbridge

### **12.3 KEY ENVIRONMENTAL ISSUES FOR THE COMING MONTH**

12.3.1 Key environmental issues to be considered in the coming month include:

- Implementation of dust suppression measures at all times;
- Potential wastewater quality impact due to surface runoff;
- Potential fugitive dust impact due to the dry/loose/exposure soil surface/dusty material;
- Ensure dust suppression measures are implemented properly;
- Sediment catch-pits and silt removal facilities should be regularly maintained;
- Management of chemical wastes;
- Site effluent discharge to the nearby nullah is prohibited;
- Follow-up of improvement on general waste management issues; and
- Implementation of construction noise preventative control measures



### 13 CONCLUSIONS AND RECOMMENDATIONS

#### 13.1 CONCLUSIONS


- 13.1.1 This is 37<sup>th</sup> monthly EM&A report presenting the monitoring results and inspection findings for the period of 1 to 30 November 2017.
- 13.1.2 No exceedances of 24-hour TSP monitoring were recorded in the Reporting Period. However, there were five exceedances of 1-hour TSP measurements trigger in Action and Limit Level at ASR5 and ASR10 on 2, 11 and 29 November 2017. NOEs were issued to notify all relevant parties. Investigation reports for the exceedances on 2 and 11 November 2017 were submitted by the ET and concluded that the exceedances were not project related. The IR for the exceedance on 29 November 2017 was prepared by the ET and pending for the IEC review. The IR of the exceedances would be presented in the next Monthly EM&A Report (December 2017).
- 13.1.3 In last Reporting Period, the investigation reports (IR) for the exceedance of 1-hour and 24-hour TSP on 21 and 27 October 2017 were submitted by ET. After the investigation, it is concluded that the exceedances on those monitoring days were not project related.
- 13.1.4 In the Reporting Period, no noise complaint was received by RE, the Contractor, ENPO or HyD. No Action Level exceedances were therefore triggered and no NOE or the associated corrective actions were required.
- 13.1.5 Site inspection for landscape and visual was conducted on weekly basis by the Landscape Architect to ensure the compliance of the intended aims of the mitigation measures. Most of the landscape works such as planting was not yet commenced.
- 13.1.6 Establishment period for the pitcher plants was completed at the end of September 2016, the joint site completion of Establishment period visit with AFCD was undertaken on 23 September 2016 and the final pitcher plants report was submitted to AFCD on early December 2016. Therefore after 23 September 2016, only the integrity of the protection fence was checked to fulfil the EIA requirement. During each inspection, the protection mitigation measures were checking at the final receptor area to make sure no site activities was undertaken inside the protection zone. Besides, no construction activities were observed to be carried out at the surrounding of the final receptor area. The condition of chain link fence is good and no repair or maintenance is required.
- 13.1.7 Landfill gas monitoring was conducted at the TD1 and Lung Mun Road works area. The monitoring results shown no exceedances were triggered.
- 13.1.8 In the Reporting Period, no environmental complaint was received.
- 13.1.9 In the last reporting period (1 to 31 October 2017), there was a complaint regarding light nuisance created by Tuen Mun - Chek Lap Kok Link Project during mid-night. The investigation report (IR) has been submitted by ET and concluded that the complaint was not project related.
- 13.1.10 No notifications of summons, or successful prosecution were received by the Contractor during the Reporting Period.
- 13.1.11 In the Reporting Period, joint site inspection by the RE, ET and the Contractor was carried out on 7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> November 2017 and the IEC has attended the joint site inspection on 28<sup>th</sup> November 2017. No non-compliance was recorded during the site inspection but 1 observation and 4 reminders were recorded.
- 13.1.12 In the Reporting Period, Grave G1 of inspection was undertaken on 7<sup>th</sup>, 14<sup>th</sup>, 21<sup>st</sup> and 28<sup>th</sup> November 2017. Based on the inspection findings, the cultural heritage mitigation measures as implemented by the Contractor are fully complied with the EM&A Manual requirements.

**13.2 RECOMMENDATIONS**

- 13.2.1 During dry season, air quality mitigation measures such as watering of site area for 12 times per day and covering of exposed slopes should be fully implemented to reduce construction dust impact as recommended in the EMIS.
- 13.2.2 Moreover, muddy water or other water pollutants from site surface runoff into the public areas will be key environment issue. Special attention should be paid on the water quality mitigation measures to prevent surface runoff flow to public area.
- 13.2.3 Stagnant water should be removed as soon as possible after rain to prevent mosquito breeding on site.

## **Appendix A**

### **Project Layout Plan**

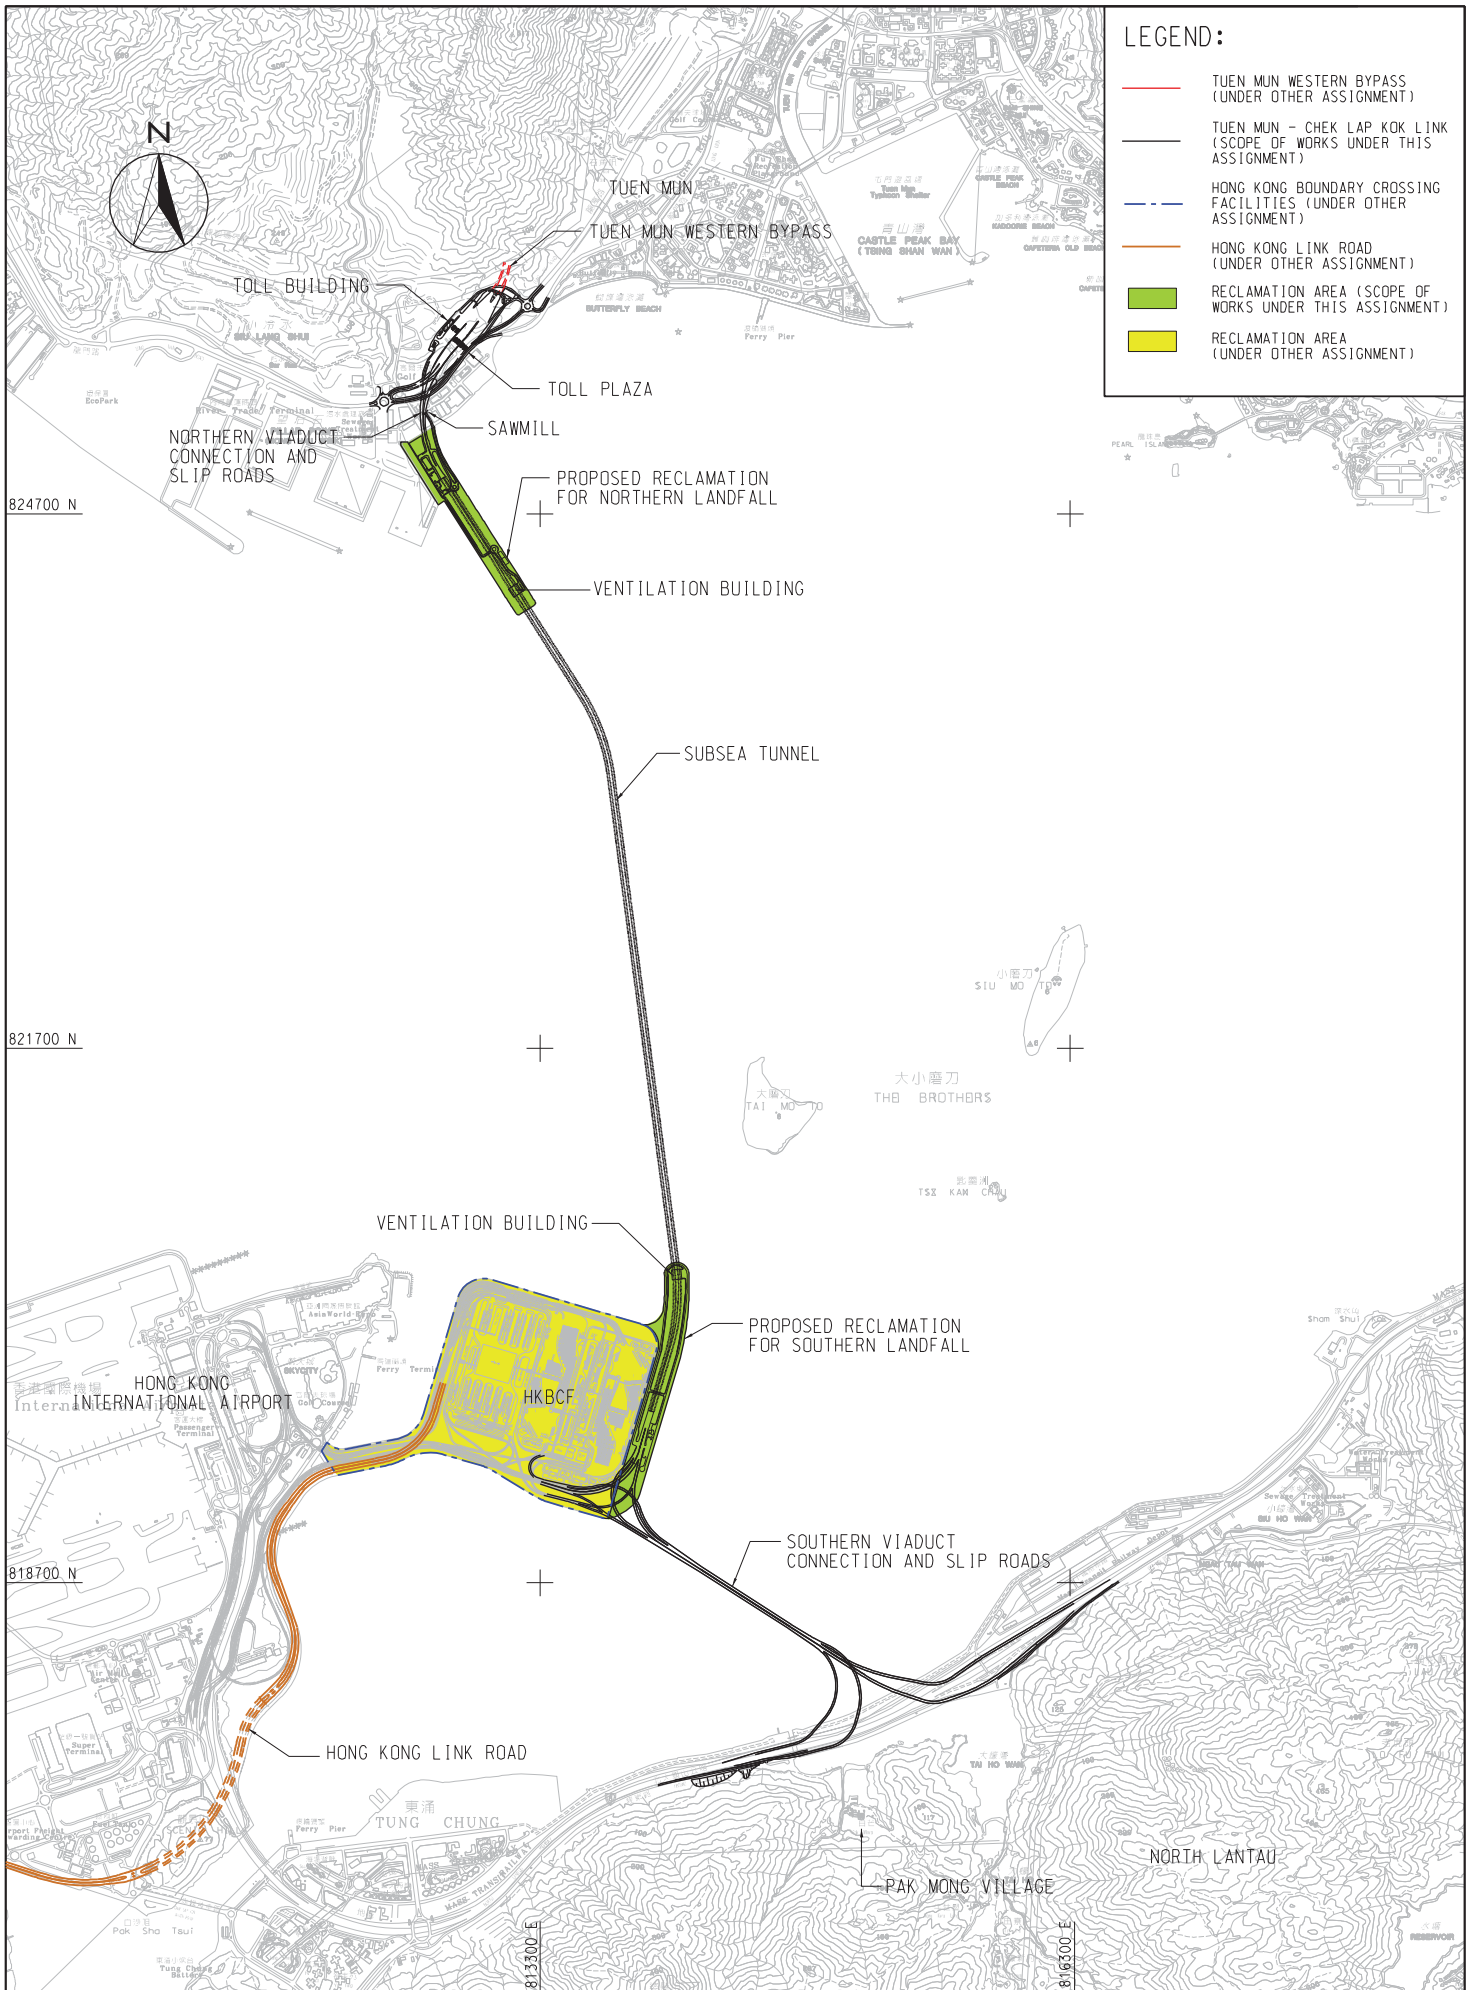

**LEGEND:**

- TUEN MUN WESTERN BYPASS (UNDER OTHER ASSIGNMENT)
- TUEN MUN - CHEK LAP KOK LINK (SCOPE OF WORKS UNDER THIS ASSIGNMENT)
- HONG KONG BOUNDARY CROSSING FACILITIES (UNDER OTHER ASSIGNMENT)
- HONG KONG LINK ROAD (UNDER OTHER ASSIGNMENT)
- RECLAMATION AREA (SCOPE OF WORKS UNDER THIS ASSIGNMENT)
- RECLAMATION AREA (UNDER OTHER ASSIGNMENT)

PROJECT NO. 60044963

**AECOM**


AGREEMENT NO. CE 52/2007(HY)  
 TUEN MUN - CHEK LAP KOK LINK - INVESTIGATION  
 GENERAL LAYOUT OF TM-CLKL

SCALE	A3 1:30000	DATE	JUL. 2009
CHECK	--	DRAWN	WYP
JOB No.	60044963	DRAWING No.	Fig 2.1
		REV	A

**Appendix B**

**Layout Plan of the Contract**

Project Management Initials: Designer: PI Checked: ALCF Approved: CWN ISO A1 594mm x 841mm  
 Plot File by: LINDO 2014/05/19 PATH: P:\Projects\60240249\DRAWING\CONTRACT\C3\1005C3\_05E1.dgn

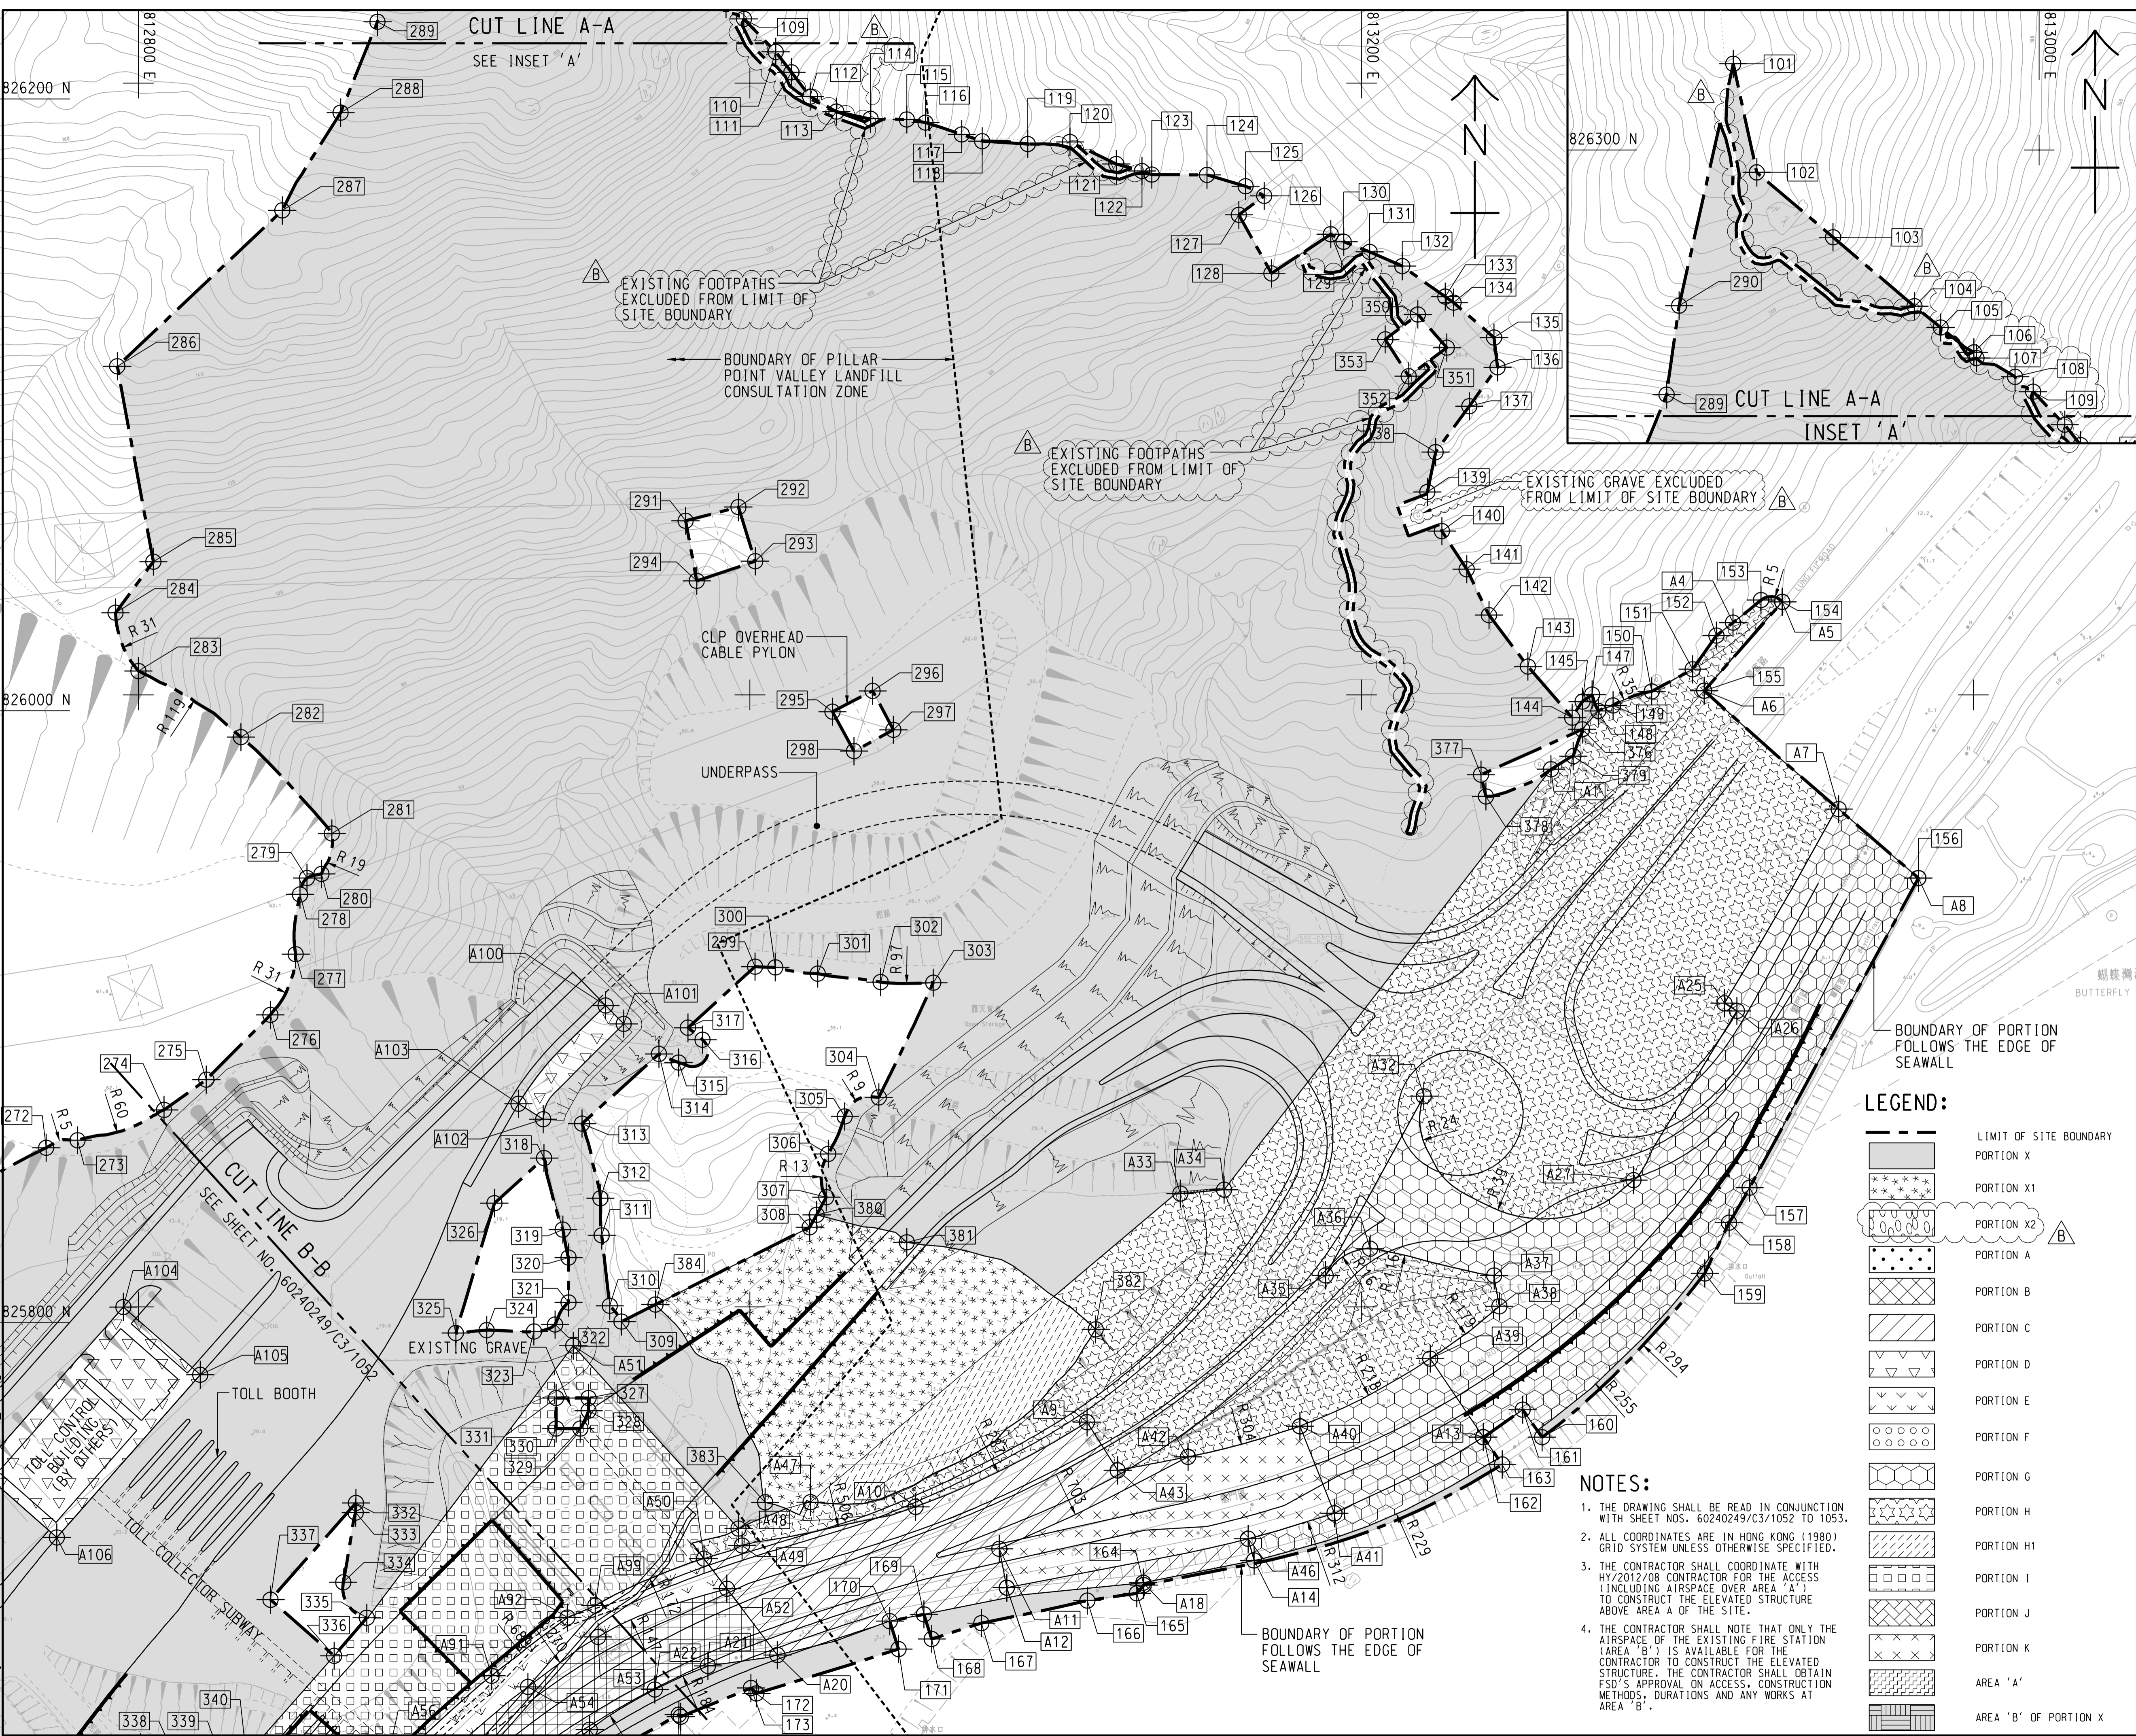

**AECOM**

**PROJECT**  
項目  
**TUEN MUN - CHEK LAP KOK LINK**

**CONTRACT TITLE**  
TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

**CLIENT**  
業主  
路政署  
**HIGHWAYS DEPARTMENT**  
港務大樓香港工程管理處  
Hong Kong - Zhuhai - Macao Bridge  
Hong Kong Project Management Office

**CONSULTANT**  
工程顧問公司  
AECOM Asia Company Ltd.  
www.aecom.com

**SUB-CONSULTANTS**  
分判工程顧問公司

**ISSUE/REVISION**  
修訂


I/R	DATE	DESCRIPTION	CHK.
B	MAR. 14	TENDER ADDENDUM NO. 2	CWN
A	FEB. 14	TENDER ADDENDUM NO. 1	CWN
-	JAN. 14	TENDER DRAWING	CWN

**STATUS**  
階段

**SCALE**  
比例  
A1 1:1000

**DIMENSION UNIT**  
尺寸單位  
METRES

**KEY PLAN**  
索引圖  
1:50000

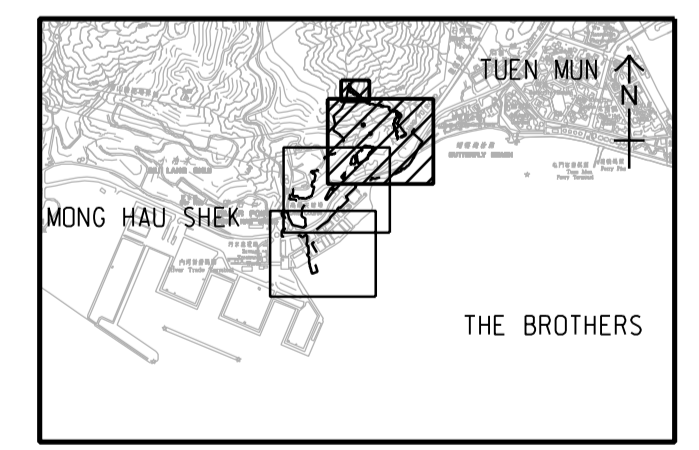

**PROJECT NO.**  
項目編號  
60240249

**CONTRACT NO.**  
合約編號  
HY/2013/12

**SHEET TITLE**  
圖紙名稱  
**PORTIONS OF SITE AND SITE BOUNDARY SETTING OUT PLAN**

**SHEET NUMBER**  
圖紙編號  
60240249/C3/1051B


SHEET 1 OF 3

- NOTES:**
1. THE DRAWING SHALL BE READ IN CONJUNCTION WITH SHEET NOS. 60240249/C3/1052 TO 1053.
  2. ALL COORDINATES ARE IN HONG KONG (1980) GRID SYSTEM UNLESS OTHERWISE SPECIFIED.
  3. THE CONTRACTOR SHALL COORDINATE WITH HY/2012/08 CONTRACTOR FOR THE ACCESS (INCLUDING AIRSPACE OVER AREA 'A') TO CONSTRUCT THE ELEVATED STRUCTURE ABOVE AREA A OF THE SITE.
  4. THE CONTRACTOR SHALL NOTE THAT ONLY THE AIRSPACE OF THE EXISTING FIRE STATION (AREA 'B') IS AVAILABLE FOR THE CONTRACTOR TO CONSTRUCT THE ELEVATED STRUCTURE. THE CONTRACTOR SHALL OBTAIN FSD'S APPROVAL ON ACCESS, CONSTRUCTION METHODS, DURATIONS AND ANY WORKS AT AREA 'B'.

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. All measurements must be obtained from the stated dimensions.

SETTING OUT COORDINATES OF SITE BOUNDARY

SETTING OUT POINT	COORDINATES	
	EASTING	NORTHING
101	812900.000	826328.165
102	812907.687	826292.657
103	812932.657	826271.462
104	812959.255	826248.939
105	812967.809	826241.968
106	812978.687	826233.842
107	812979.543	826231.975
108	812992.172	826225.845
109	812998.046	826220.987
110	813008.394	826210.180
111	813013.551	826203.523
112	813019.680	826195.595
113	813028.256	826190.669
114	813039.418	826188.327
115	813051.242	826188.103
116	813057.382	826187.067
117	813069.235	826183.229
118	813075.914	826180.992
119	813090.821	826180.083
120	813104.589	826180.783
121	813119.757	826173.560
122	813128.170	826171.228
123	813131.357	826170.082
124	813149.404	826169.990
125	813162.041	826166.283
126	813168.123	826163.136
127	813159.825	826156.924
128	813170.488	826137.774
129	813189.868	826150.598
130	813194.079	826148.129

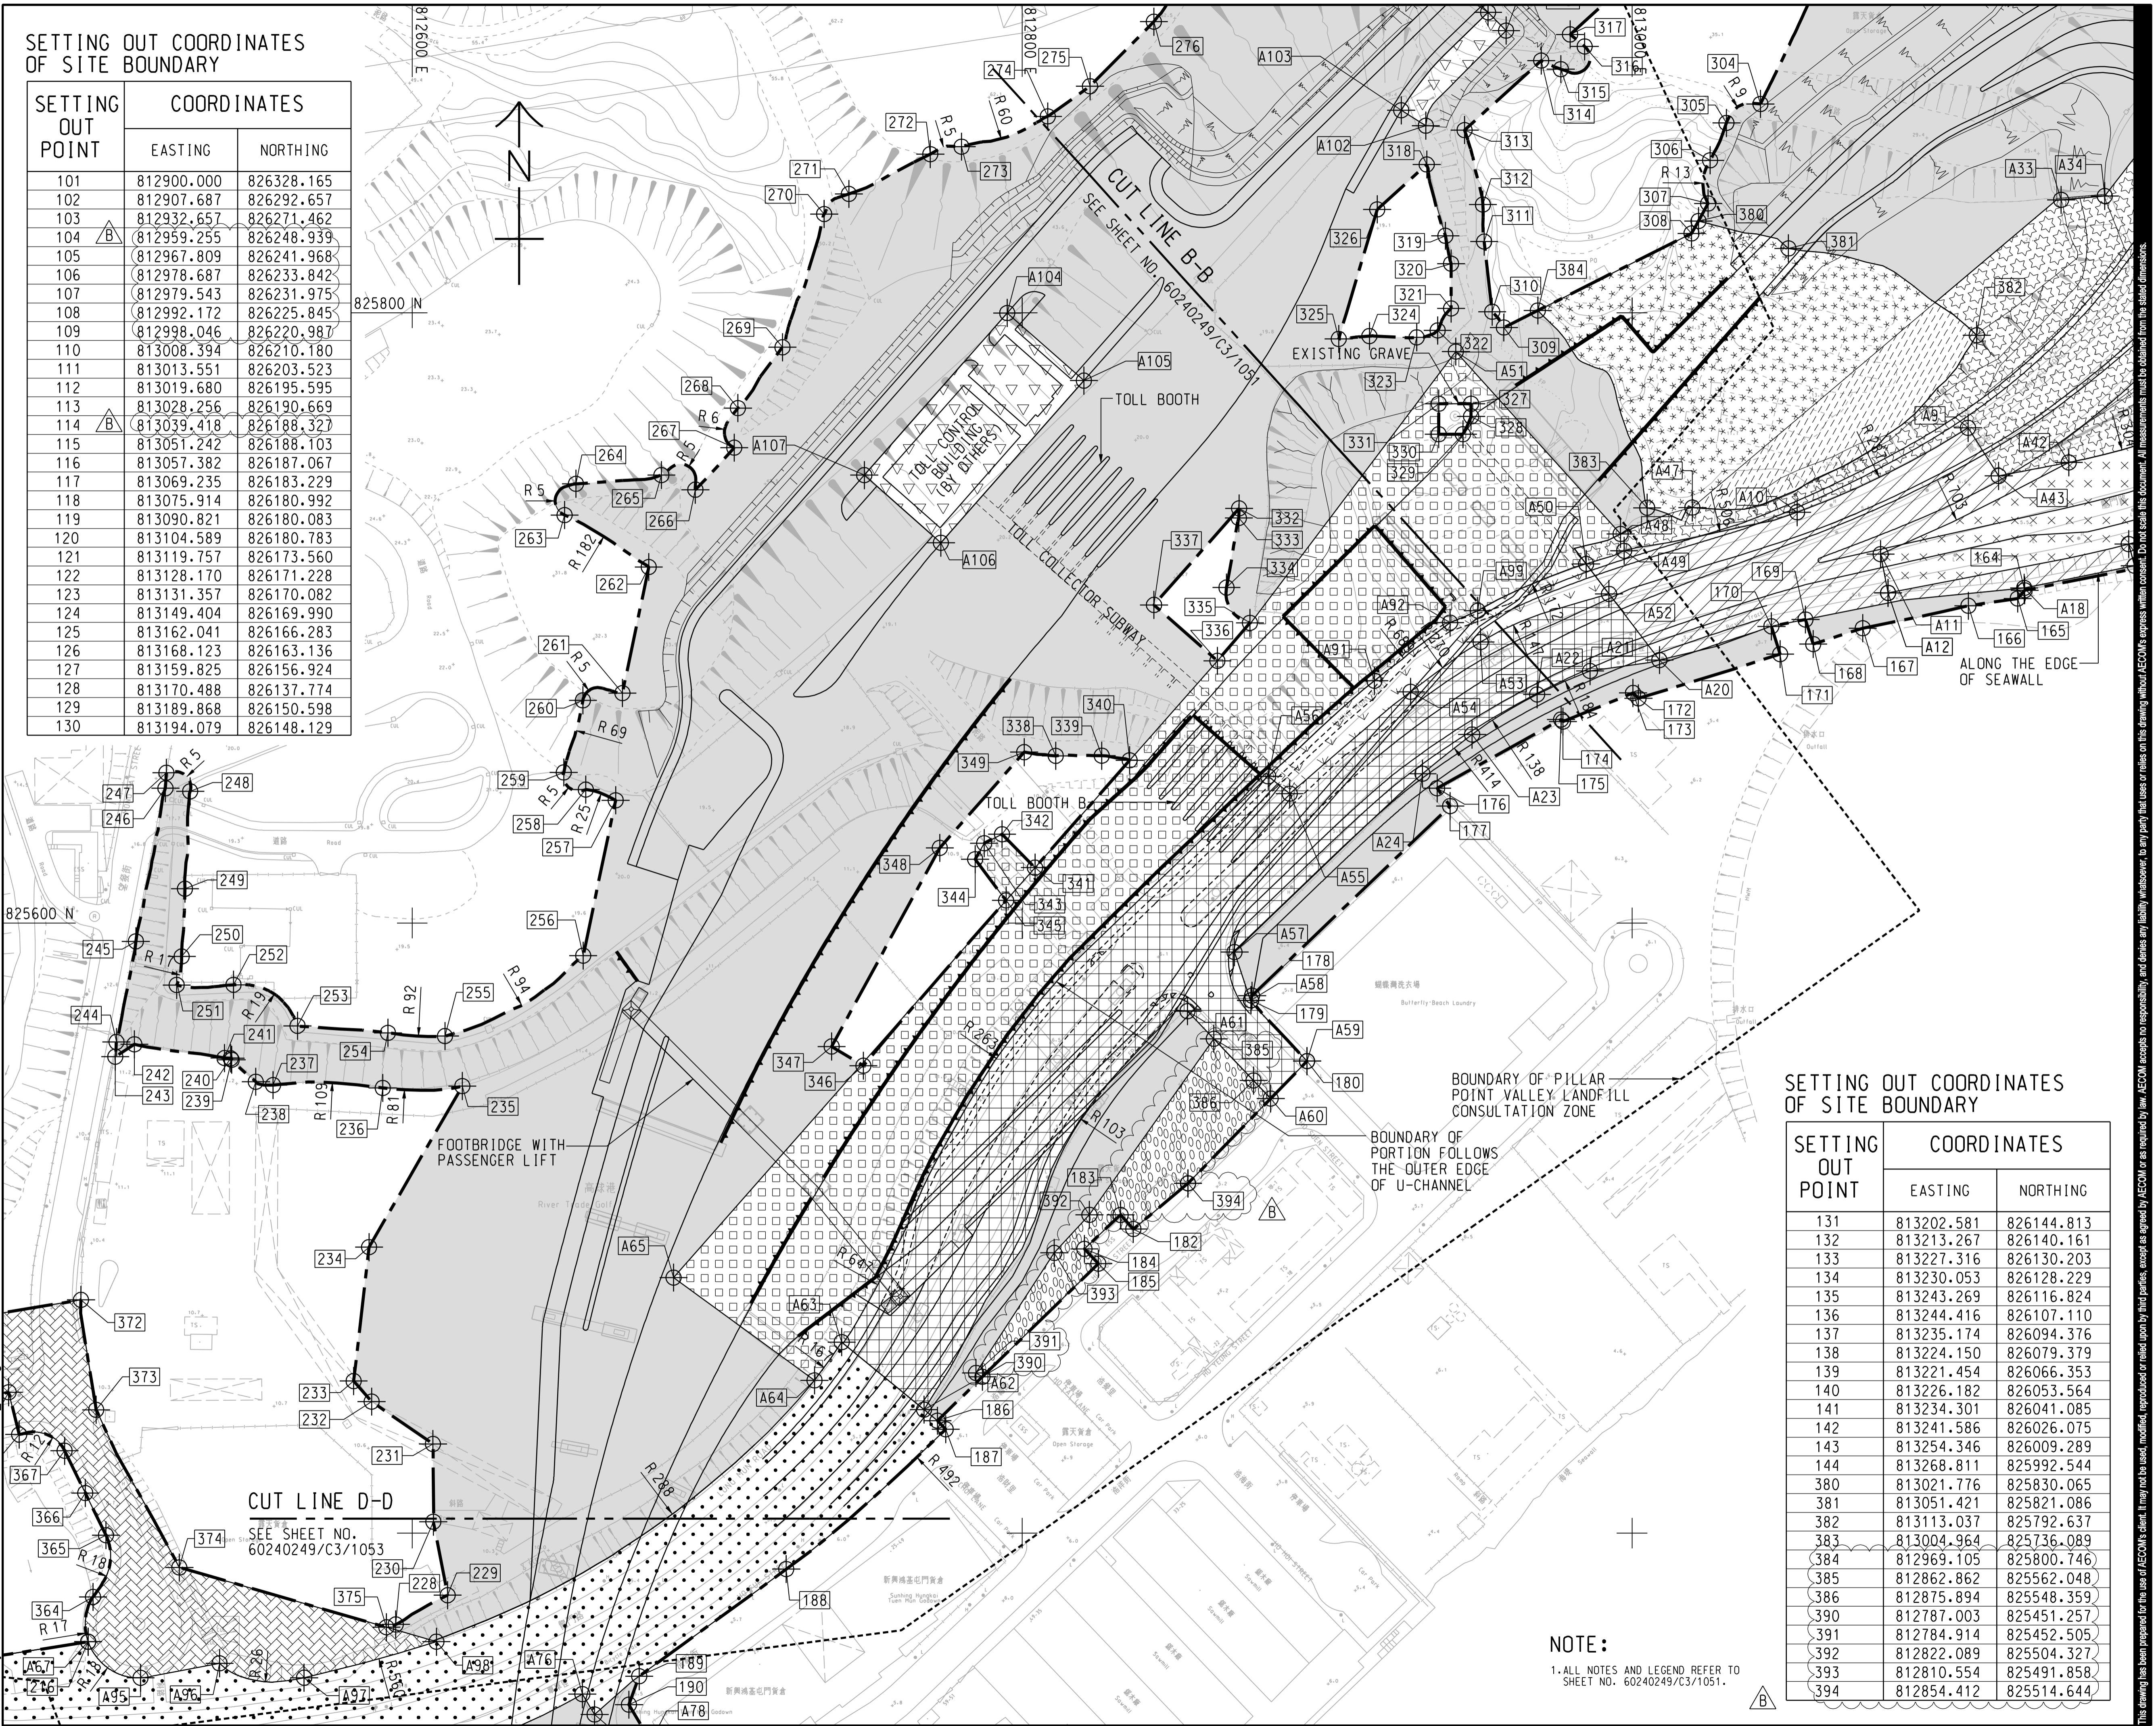

SETTING OUT COORDINATES OF SITE BOUNDARY

SETTING OUT POINT	COORDINATES	
	EASTING	NORTHING
131	813202.581	826144.813
132	813213.267	826140.161
133	813227.316	826130.203
134	813230.053	826128.229
135	813243.269	826116.824
136	813244.416	826107.110
137	813235.174	826094.376
138	813224.150	826079.379
139	813221.454	826066.353
140	813226.182	826053.564
141	813234.301	826041.085
142	813241.586	826026.075
143	813254.346	826009.289
144	813268.811	825992.544
380	813021.776	825830.065
381	813051.421	825821.086
382	813113.037	825792.637
383	813004.964	825736.089
384	812969.105	825800.746
385	812862.862	825562.048
386	812875.894	825548.359
390	812787.003	825451.257
391	812784.914	825452.505
392	812822.089	825504.327
393	812810.554	825491.858
394	812854.412	825514.644

NOTE:  
1. ALL NOTES AND LEGEND REFER TO SHEET NO. 60240249/C3/1051.



PROJECT  
TUEN MUN - CHEK LAP KOK LINK

CONTRACT TITLE  
TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

CLIENT  
路政署  
HIGHWAYS DEPARTMENT  
港務大樓香港工程管理局  
Hong Kong - Zhuhai - Macao Bridge  
Hong Kong Project Management Office

CONSULTANT  
AECOM Asia Company Ltd.  
www.aecom.com

SUB-CONSULTANTS  
分列工程顧問公司

ISSUE/REVISION


I/R	DATE	DESCRIPTION	CHK.
B	MAR. 14	TENDER ADDENDUM NO. 2	CWN
A	FEB. 14	TENDER ADDENDUM NO. 1	CWN
-	JAN. 14	TENDER DRAWING	CWN

STATUS

擬定

SCALE  
比例  
A1 1:1000  
DIMENSION UNIT  
尺寸單位  
METRES

KEY PLAN  
索引圖  
1:50000

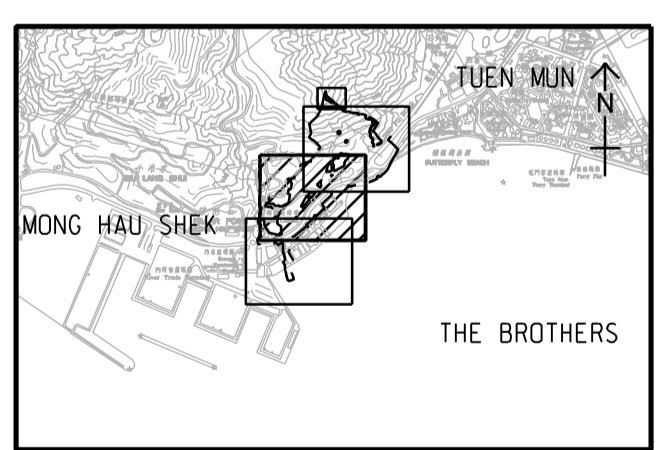


PROJECT NO.  
項目編號  
60240249  
CONTRACT NO.  
合約編號  
HY/2013/12

SHEET TITLE  
圖紙名稱  
PORTIONS OF SITE AND SITE BOUNDARY SETTING OUT PLAN  
SHEET 2 OF 3

SHEET NUMBER  
圖紙編號  
60240249/C3/1052B

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, for any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.

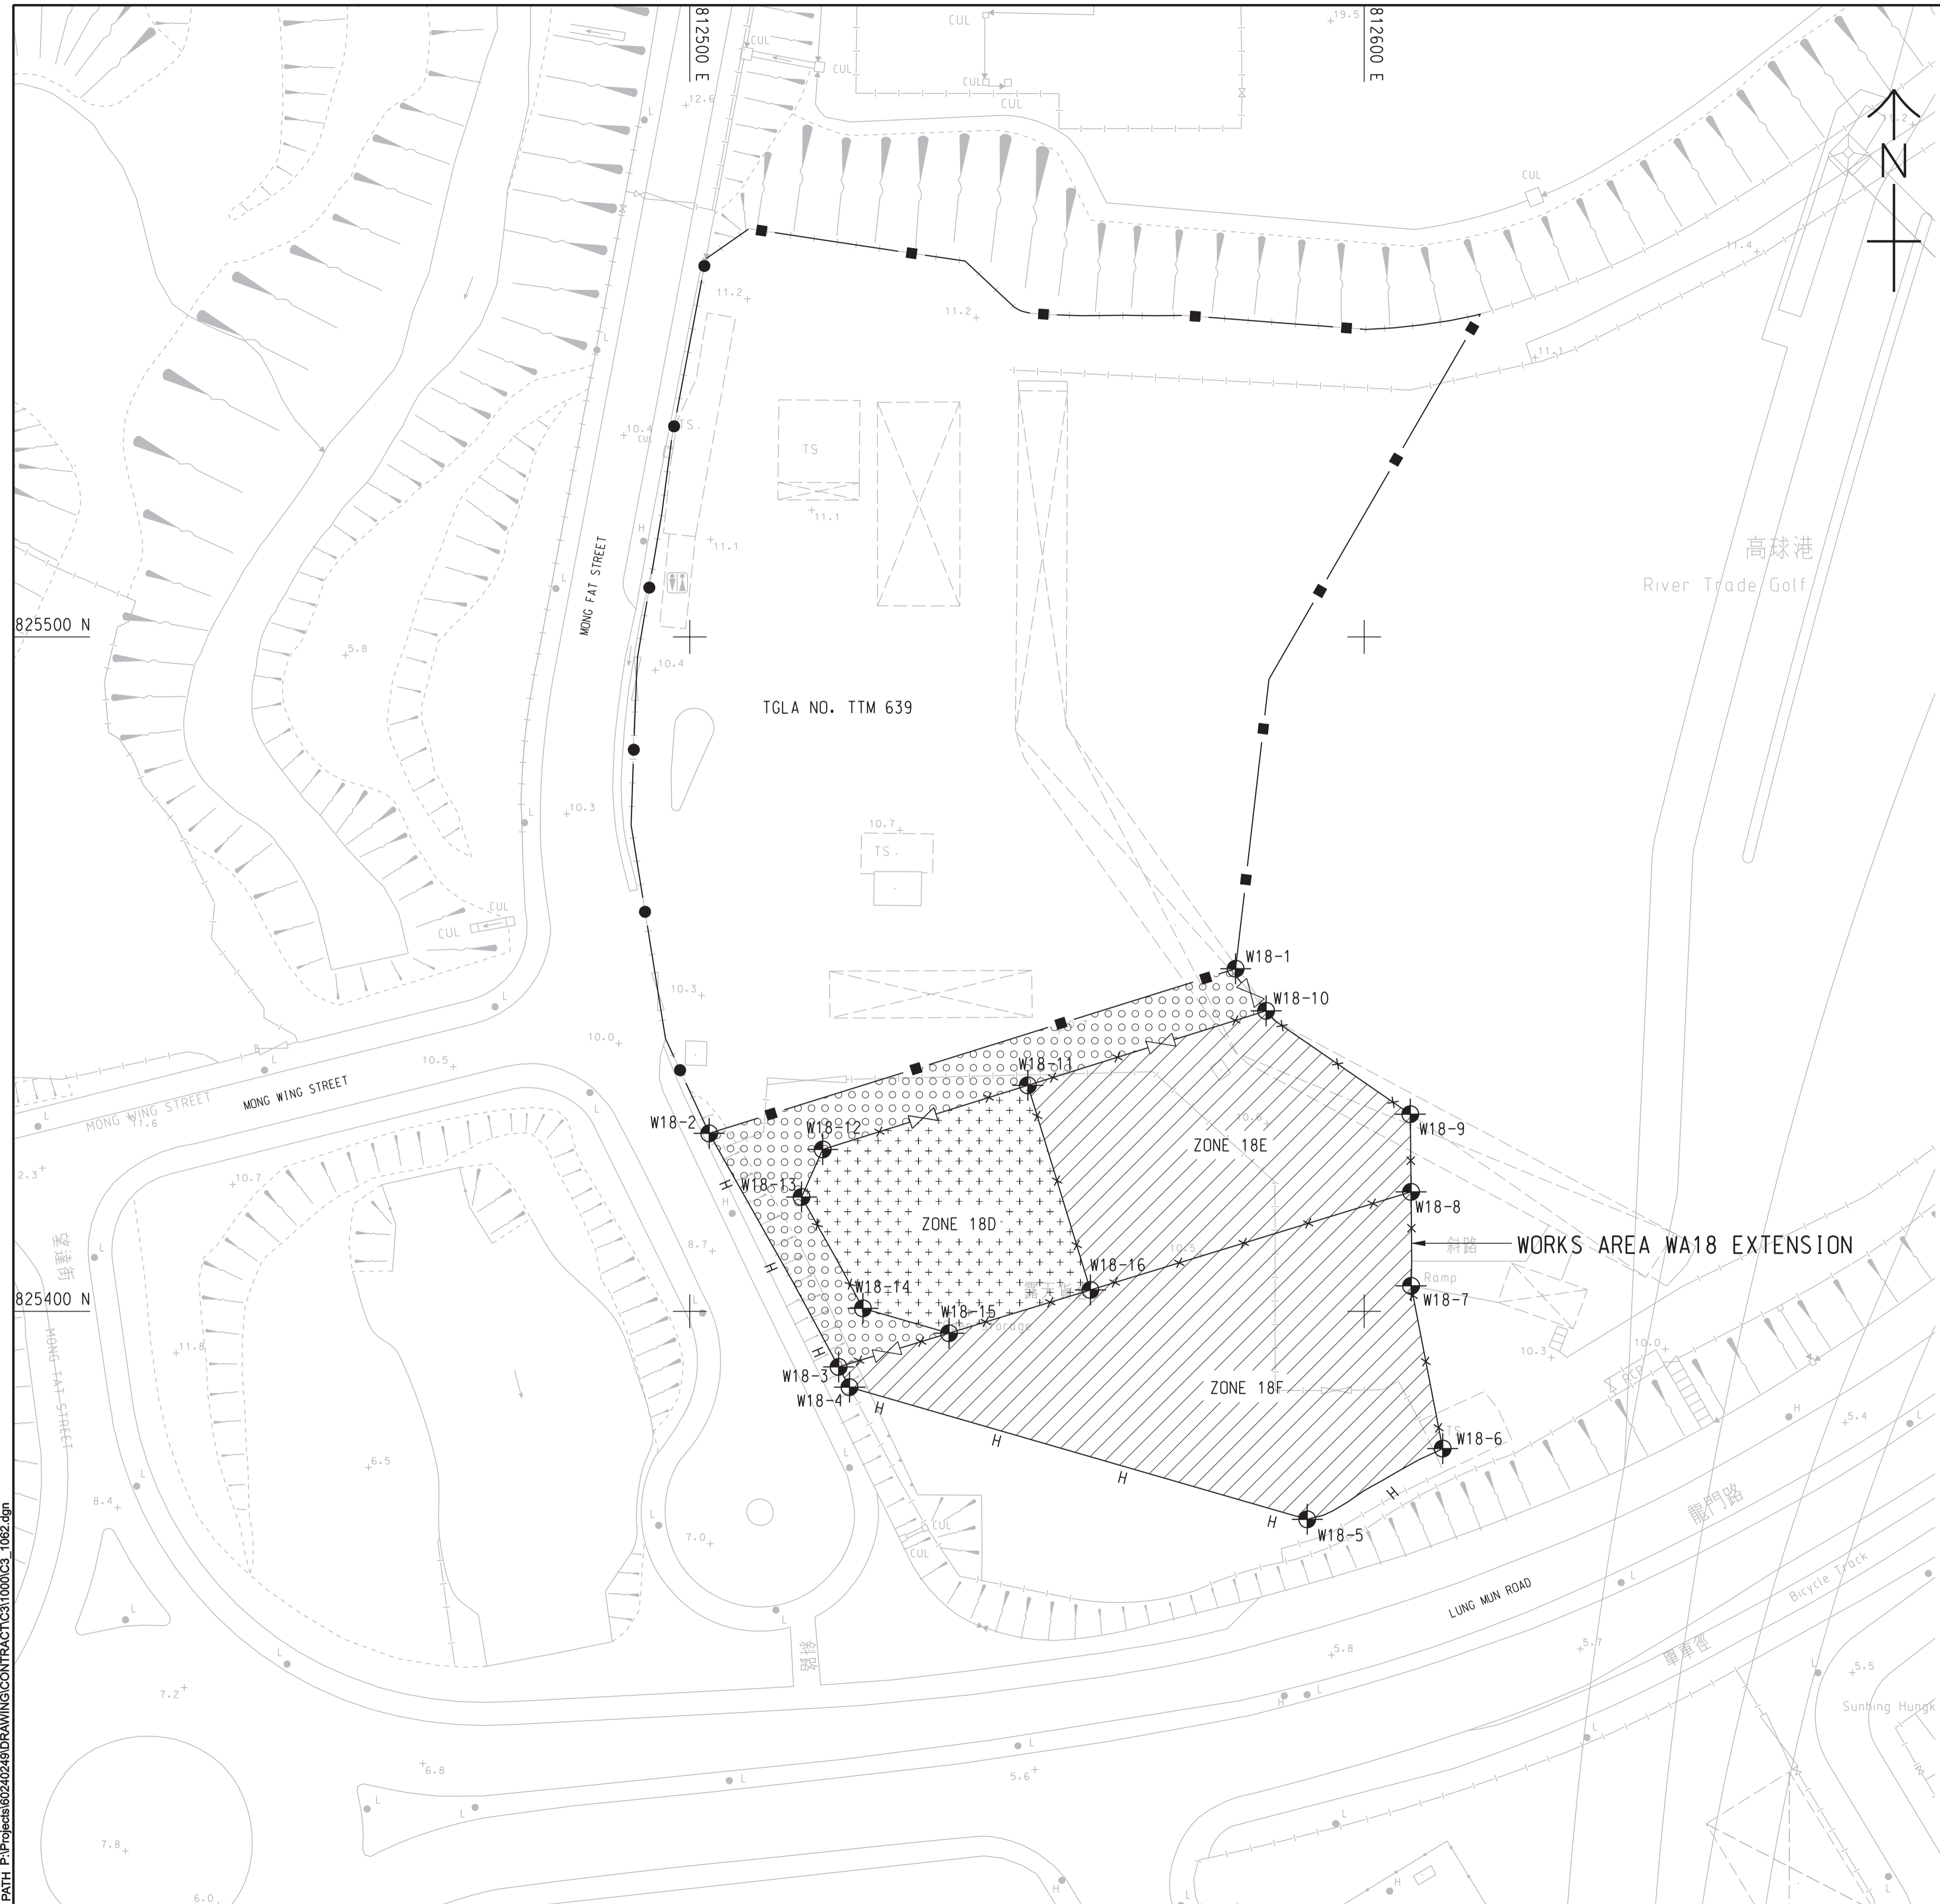

**NOTES:**

- THIS DRAWING SHALL BE READ IN CONJUNCTION WITH THE WORKS AREA KEY PLAN IN SHEET NO. 60240249/C3/1000.
- DEMARCATON OF THE WORKS AREA SHALL BE DETERMINED ON SITE.
- REFER TO HIGHWAYS DEPARTMENT STANDARD DRAWING NOS. H6110 AND H6111 FOR DETAILS OF HOARDING.
- REFER TO HIGHWAYS DEPARTMENT STANDARD DRAWING NOS. H6121 AND H6122 FOR DETAILS OF CHAIN LINK FENCE.
- REFER TO HIGHWAYS DEPARTMENT STANDARD DRAWING NO. H6121 FOR DETAILS OF GATE.
- CHAIN LINK FENCE SHALL BE ERRECTED ALONG THE WORKS AREA BOUNDARY. THE ALIGNMENT AND EXTENT OF HOARDING AND CHAIN LINK FENCE SHOWN ARE INDICATIVE ONLY AND SHALL BE CONFIRMED BY THE ENGINEER.
- THE LOCATION AND WIDTH OF GATE SHOWN ARE INDICATIVE ONLY AND SHALL BE CONFIRMED BY THE ENGINEER.
- THE SETTING OUT INFORMATION AND WORKS AREA CONDITIONS SHOWN IN THIS DRAWING ARE FOR REFERENCE ONLY. THE WORKS AREA BOUNDARY SHALL BE IN ACCORDANCE WITH THE ENGINEERING CONDITIONS FOR TEMPORARY GOVERNMENT LAND ALLOCATION NO. GLA-TM 639. IN CASE OF DISCREPANCY BETWEEN THE BOUNDARY SHOWN ON THIS DRAWING AND THE BOUNDARY INDICATED ON THE ENGINEERING CONDITIONS, THE LATTER SHALL PREVAIL.
- THE WORKS AREAS SHOWN ON THIS DRAWING ARE TO BE SHARED-USED AMONG THE TM-CLKL RELATED CONTRACTS. THE AREAS HATCHED WITH ARE TENTATIVELY ALLOCATED FOR THE USE BY THE CONTRACT.
- THE COMMON AREA SHALL BE CONCRETE PAVED BY THE CONTRACTOR.
- ZONE 18F SHALL BE USED FOR THE SITE ACCOMMODATION OF THE ENGINEER. ZONE 18E SHALL BE USED FOR SITE ACCOMMODATION OF THE CONTRACTOR.
- ZONE 18D IS TO BE USED BY THE CONTRACTOR OF CONTRACT NO. HY/2012/08-TUEN MUN-CHEK LAP KOK LINK-NORTHERN CONNECTION SUB-SEA TUNNEL SECTION TO STORE PLANT AND EQUIPMENT ASSOCIATED WITH THE TBM TUNNELS FROM THE DATE FOR COMMENCEMENT OF THE WORKS TO 126 DAYS FROM THE DATE FOR COMMENCEMENT OF THE WORKS. THE CONTRACTOR SHALL LIAISE AND PROVIDE FREE AND UNOBSTRUCTED 24-HOUR ACCESS FOR THE CONTRACTOR OF CONTRACT NO. HY/2012/08 TO ZONE 18D. THE CONTRACTOR SHALL BE GIVEN THE POSSESSION OF ZONE 18D IN ACCORDANCE WITH APPENDIX TO FORM OF TENDER-P.3.

**LEGEND:**

- WORKS AREA FOR THE CONTRACT
- COMMON AREA (MAINTAINED UNDER THE CONTRACT) TO BE SHARED-USED WITH OTHER CONTRACTS
- AREA TO BE USED BY THE CONTRACTOR OF CONTRACT NO. HY/2012/08 AND WORKS AREA FOR THIS CONTRACT TO BE EARLY HANDED OVER BY THE CONTRACTOR (SEE NOTES NO. 12 ABOVE)
- HOARDING AND GATE (TO BE ERRECTED AND MAINTAINED UNDER THIS CONTRACT)
- EXISTING CHAIN LINK FENCE MAINTAINED BY OTHERS
- CHAIN LINK FENCE AND GATE (TO BE ERRECTED AND MAINTAINED UNDER THIS CONTRACT)
- EXISTING HOARDING AND GATE MAINTAINED BY OTHERS

**SETTING OUT CO-ORDINATES OF WORKS AREA WA18 EXTENSION**

POINT	CO-ORDINATES	
	EASTING	NORTHING
W18-1	812580.934	825450.791
W18-2	812502.880	825426.380
W18-3	812522.068	825391.750
W18-4	812523.679	825388.756
W18-5	812591.556	825369.151
W18-6	812611.638	825379.647
W18-7	812606.954	825403.769
W18-8	812606.951	825417.705
W18-9	812606.832	825429.231
W18-10	812585.456	825444.557
W18-11	812550.126	825433.508
W18-12	812519.715	825423.997
W18-13	812516.580	825416.947
W18-14	812525.682	825400.438
W18-15	812538.435	825396.754
W18-16	812559.404	825403.166



**PROJECT**  
 項目  
**TUEN MUN - CHEK LAP KOK LINK**

**CONTRACT TITLE**  
 TUEN MUN - CHEK LAP KOK LINK - NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS

**CLIENT**  
 業主  
 路政署  
**HIGHWAYS DEPARTMENT**  
 港務處大樓香港工程發展處  
 Hong Kong - Zhuhai - Macao Bridge  
 Hong Kong Project Management Office

**CONSULTANT**  
 工程師有限公司  
**AECOM Asia Company Ltd.**  
 www.aecom.com

**SUB-CONSULTANTS**  
 分判工程師有限公司

**ISSUE/REVISION**

REV	DATE	DESCRIPTION	CHK.
B	MAR. 14	TENDER ADDENDUM NO. 2	CWN
A	FEB. 14	TENDER ADDENDUM NO. 1	CWN
-	JAN. 14	TENDER DRAWING	CWN

**STATUS**  
 階段

**SCALE**  
 比例  
 A1 1:500

**DIMENSION UNIT**  
 尺寸單位  
 METRES

**KEY PLAN**  
 索引圖

**PROJECT NO.**  
 項目編號  
 60240249

**CONTRACT NO.**  
 合約編號  
 HY/2013/12

**SHEET TITLE**  
 圖紙名稱  
**WORKS AREA AND HOARDING PLAN**


**SHEET NUMBER**  
 圖紙編號  
 60240249/C3/1062B

This drawing has been prepared for the use of AECOM's client. It may not be used, modified, reproduced or relied upon by third parties, except as agreed by AECOM or as required by law. AECOM accepts no responsibility, and denies any liability whatsoever, to any party that uses or relies on this drawing without AECOM's express written consent. Do not scale this document. All measurements must be obtained from the stated dimensions.



## **Appendix C**

### **Organization of the Contract**

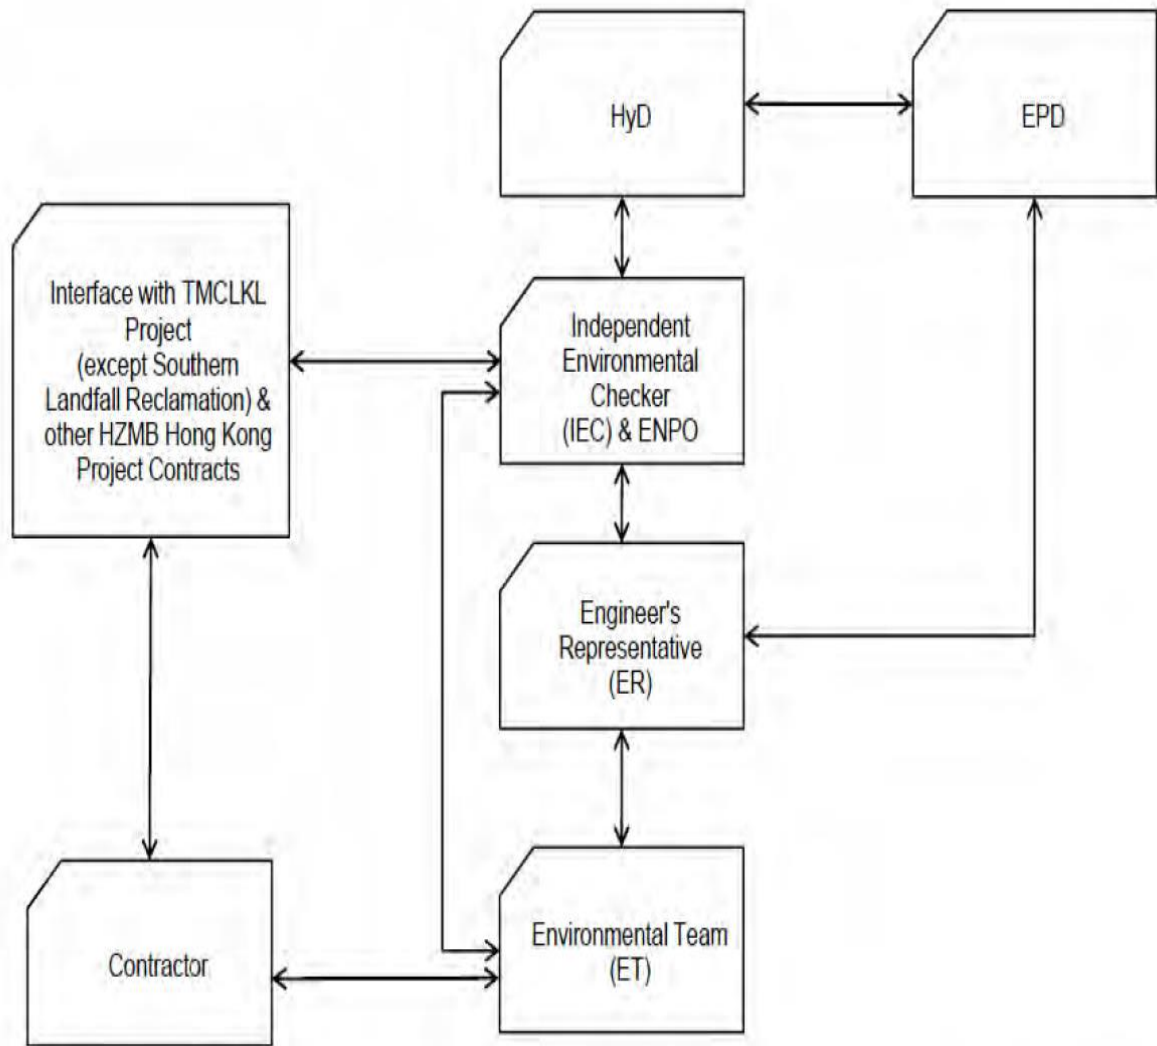

↔ Line of Communication

**Project Organization chart**

**Contact Details of Key Personnel for the Contract HY/2013/12**

<b>Organization</b>	<b>Project Role</b>	<b>Name of Key Staff</b>	<b>Tel No</b>	<b>Fax No.</b>
HyD	Employer	Mr. Stephen W.C. Chan	2762 3669	3188 6614
AECOM	Principal Resident Engineer	Mr. S.W. Fok	2218 7209	2218 7399
AECOM	Chief Resident Engineer	Mr. Albert Yu	2218 7288	2218 7399
AECOM	Resident Engineer (S&E)	Mr. Kelvin Yeung	22187289	2218 7399
Ramboll Environ	Environmental Project Office (ENPO)	Mr. YH Hui	3465 2850	3465 2899
Ramboll Environ	Independent Environmental Checker (IEC)	Dr. FC Tsang	3465 2851	3465 2899
CKJV	Deputy Project Manager	Mr. Raymond Suen	2253 8309	2253 8399
CKJV	Site Agent	Mr. Wilson Lau	2253 8300	2253 8399
CKJV	Safety and Environmental Manager	Mr. Winson Chung	2273 3185	2375 3655
CKJV	Environmental Officer	Mr. Thomas Tang	2253 8300	2253 8399
CKJV	Environmental Supervisor	Mr. Tommy Law	2253 8300	2253 8399
CKJV	Environmental Supervisor	Mr. Alex Li	2253 8300	2253 8399
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Miss Nicola Hon	2959 6059	2959 6079
AUES	Environmental Consultant	Mr. Ben Tam	2959 6059	2959 6079
HKL	Registered Landscape Architect	Kenneth Ng	2866 3903	--

**Legend:**

*HyD (Employer) – Highways Department*

*AECOM (Engineer) – AECOM Asia Co. Ltd.*

*CKJV (Main Contractor) – CRBC-Kaden Joint Venture*

*Ramboll Environ (ENPO and IEC) – Ramboll Environ Hong Kong Limited*

*AUES (ET) – Action-United Environmental Services & Consulting*

*HKL(RLA) – Hong Kong Landscape*

## **Appendix D**


### **Three-Months Rolling Programme**

Activity ID	Activity Name	2017		2018	
		Oct	Nov	Dec	Jan
<b>HY/2013/12 TMCLK Northern Connection Toll Plaza and Associated-Works Programme-Rev.4A Monthly I</b>					
<b>Site Possession Dates</b>					
PPD1140	Portion F Possession Date				
<b>Dismantling of HY/2012/04 Project Office at WA6</b>					
DM10010	Appointment of specialist subcontractor for demolition				
<b>Instrumentation and Monitoring</b>					
<b>Ground Settlement Marker</b>					
IM10110	Installation of GSM35-36,GSM44,GSM47-50(Portion F)				
<b>Piezometer/Standpipe</b>					
IM50025	GI for PADH13 and installation piezometer				
IM60030	GI for PADH14&15 and installation piezometer				
<b>Toll Plaza Decking TD1-Section 1</b>					
<b>Stage 1</b>					
<b>Field Works</b>					
<b>Deck Construction</b>					
<b>In-situ Deck and Precast Beam</b>					
TD121150	M.J installation				
<b>Parapet and Finishing Work</b>					
<b>Parapet and Railing Installation</b>					
TD120940	Parapet and planter installation				
TD120990	Railing installation and street furniture installation for TCSS and E&M installation				
<b>Toll Booth Canopy</b>					
<b>Toll both canopy and island</b>					
TD121270	Toll booth island				
TD121290	Canopy,Completion civil provision works for TCSS and E&M				
<b>Completion of Stage 1 For TD1</b>					
TD120010	Achievement of KD-1( stage 1) for TD1				
<b>Completion of TD1 in Section 1</b>					
<b>Drainage Works and Water Works</b>					
TD121000	Water works				
<b>Toll Plaza Decking TD2-Section 1</b>					
<b>Field Works</b>					
<b>Deck Construction</b>					
TD220720	Falsework removal and M.J installation				
<b>Parapet and Finishing Works</b>					
TD220210	Construct parapet ,planter and street furniture installation for TCSS and E&M installation				
TD220230	Feature groove,Completion civil provision works for TCSS and E&M				
<b>Miscellaneous Works</b>					
TD220700	Achievement of KD-1(Stage 1)for TD2				

█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ▼ Summary

**CRBC - Kaden JV  
Three-Month Rolling Programme**



Date	Revision	Checked	Approved
28-11-17	4		

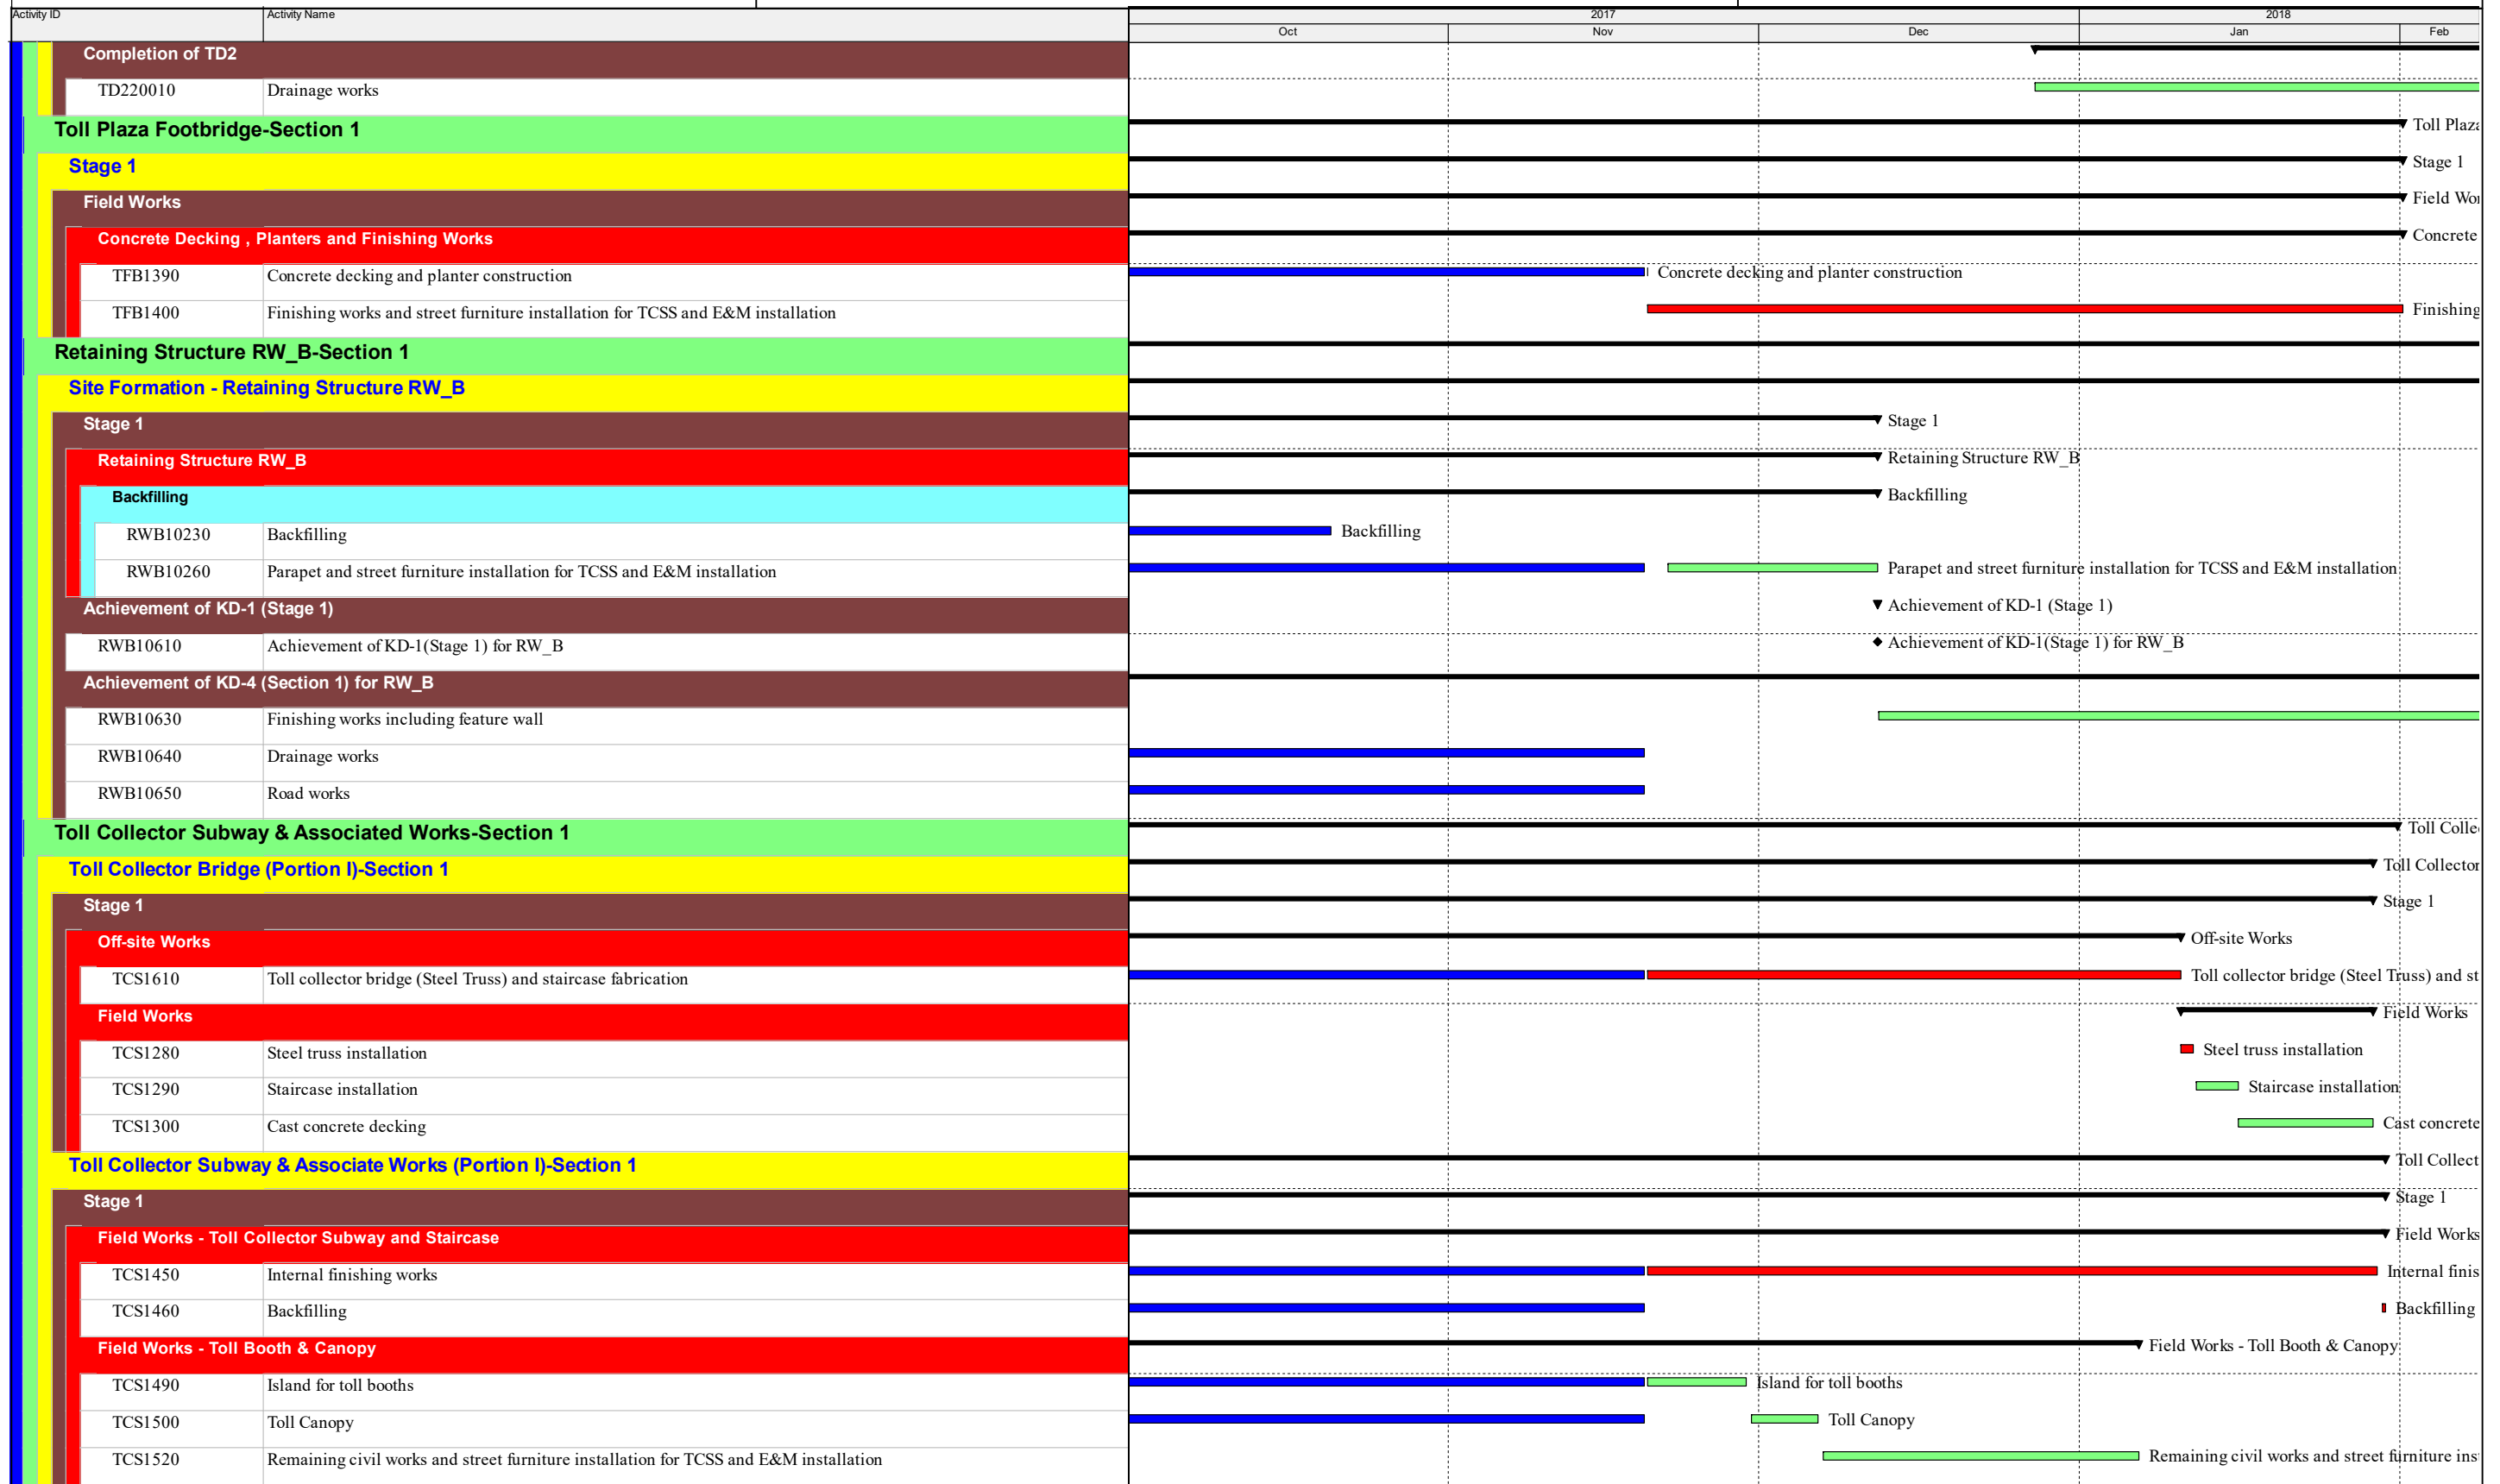

█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ▼ Summary


**CRBC - Kaden JV  
Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		

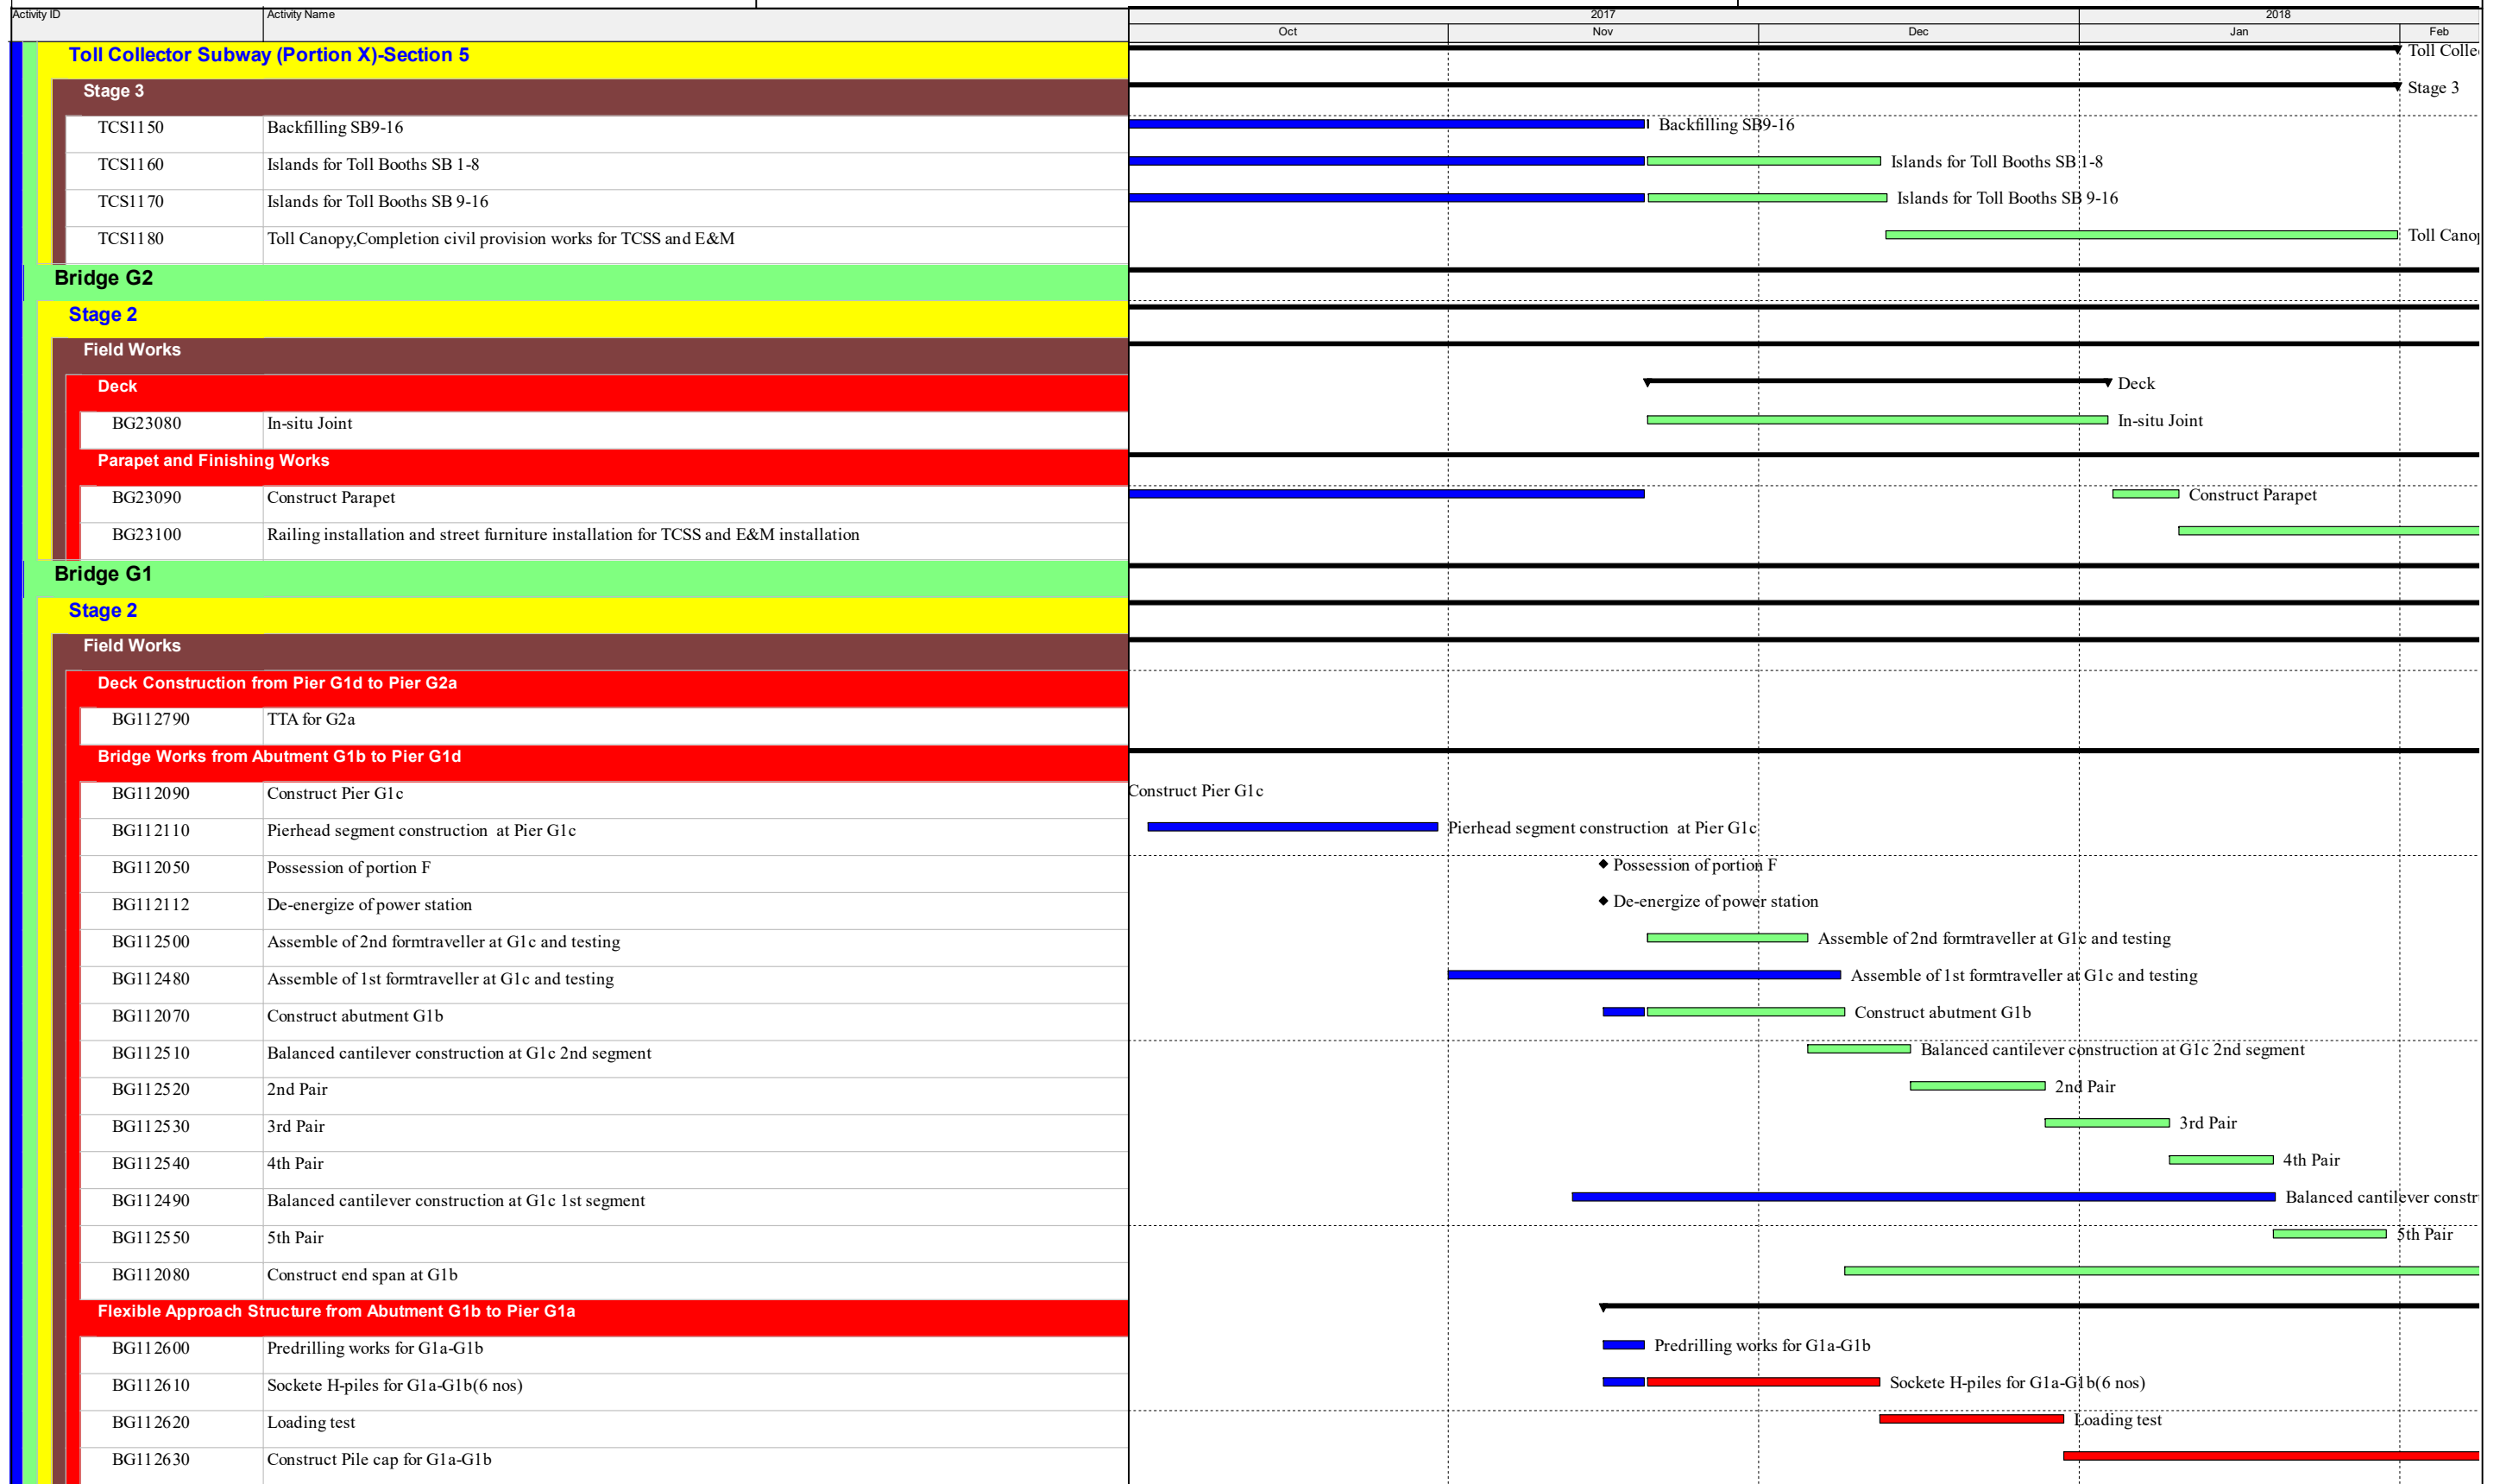

**CRBC - Kaden JV**  
**Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		

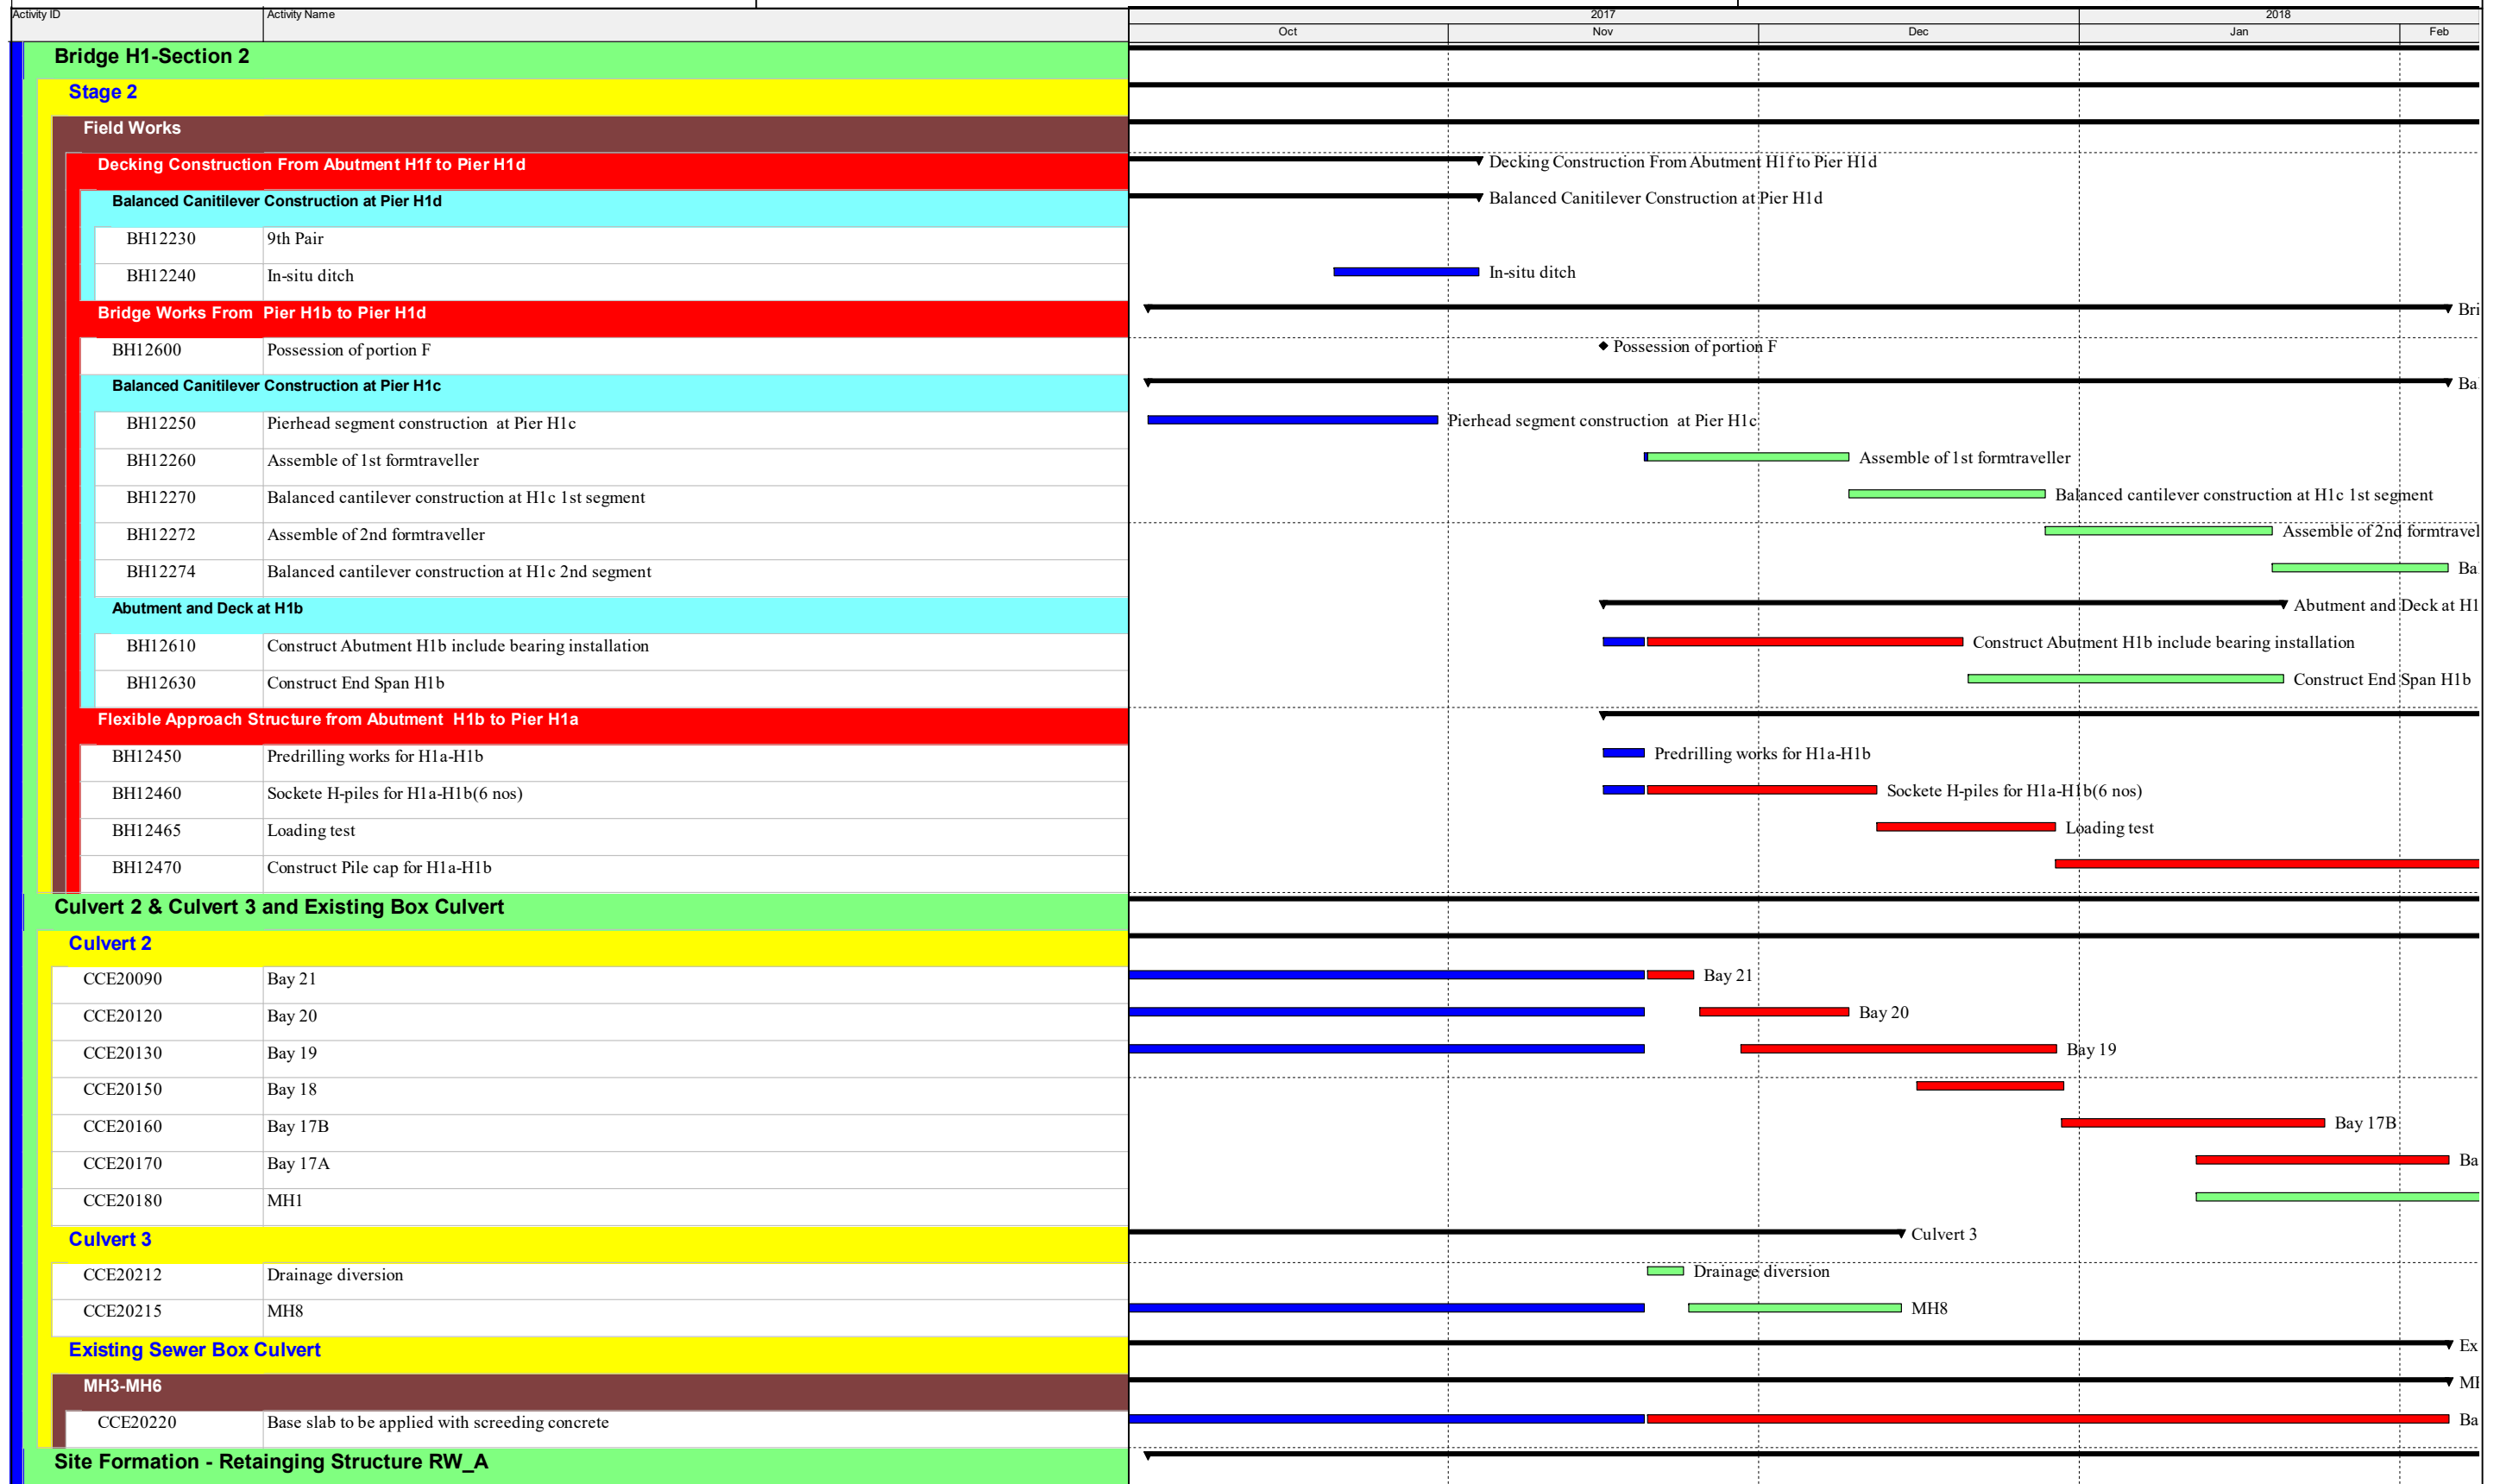


█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ▼ Summary

**CRBC - Kaden JV  
Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		



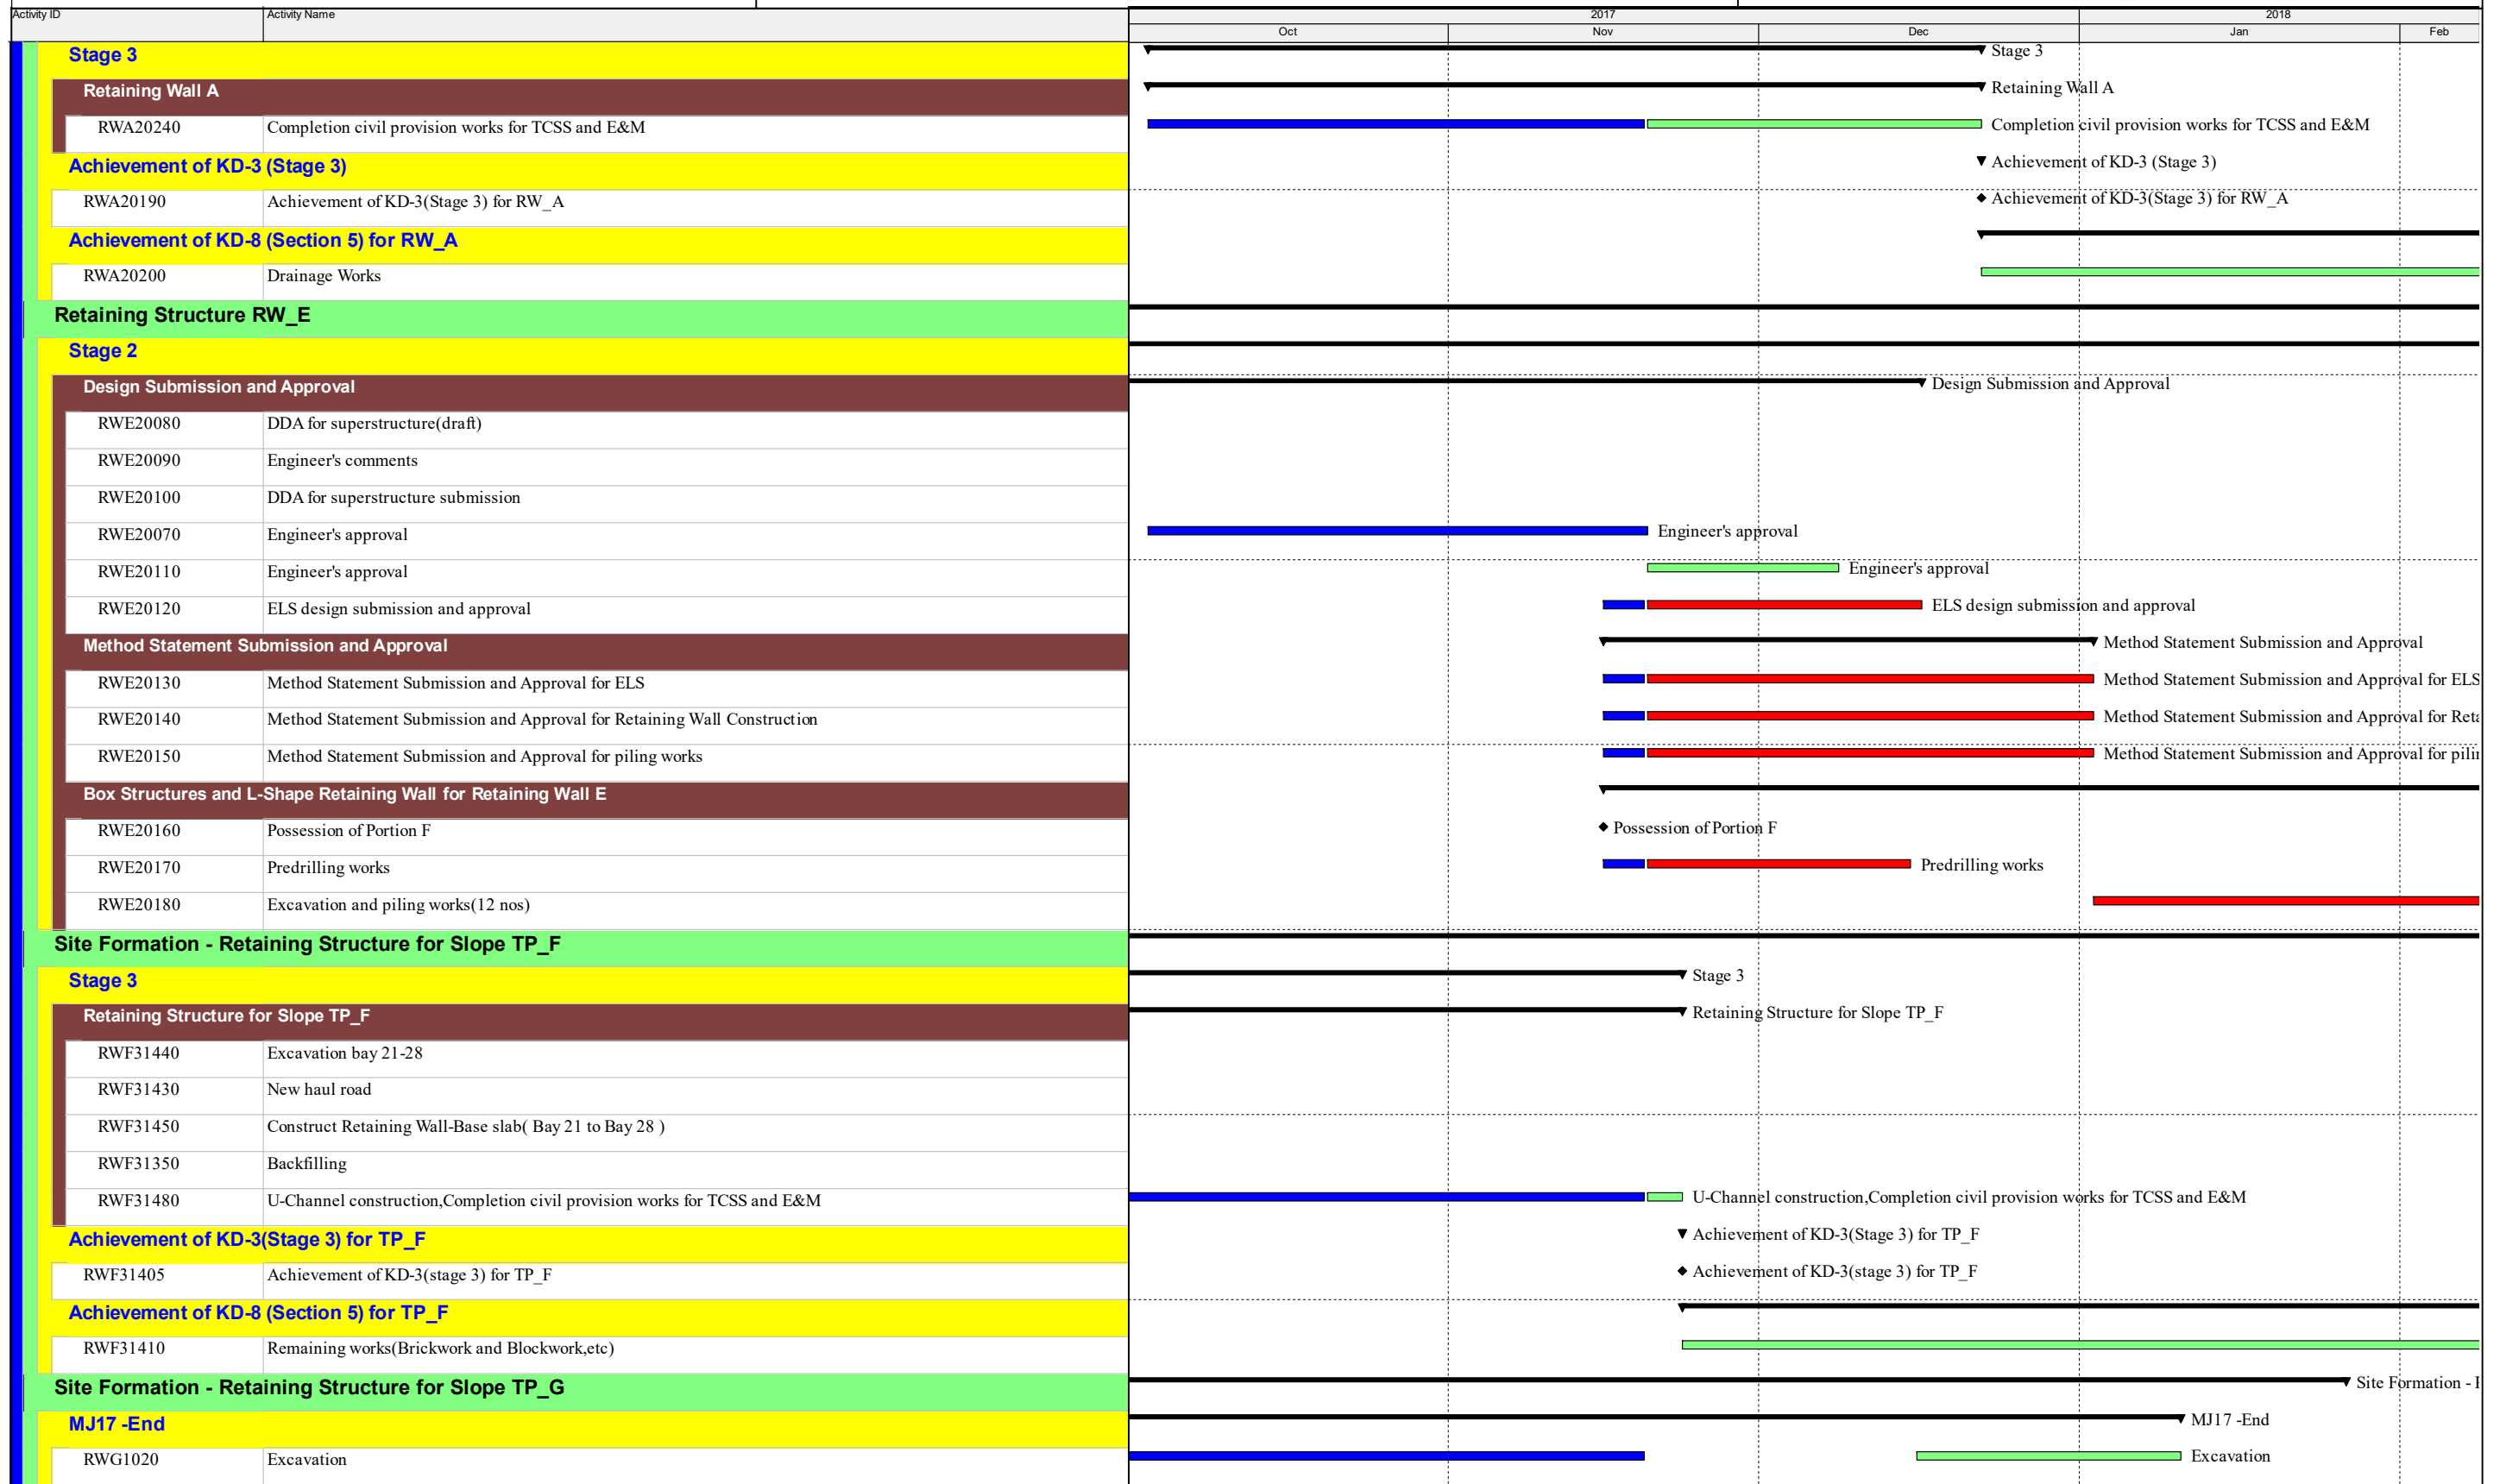

█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ▼ Summary

**CRBC - Kaden JV  
Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		

Activity ID	Activity Name	2017					2018	
		Oct	Nov	Dec	Jan	Feb		
RWG1010	G.I and Trial Pit							G.I and Trial Pit
<b>MJ16-MJ17</b>								MJ16-MJ17
RWG1070	Excavation							Excavation
<b>Site Formation - Slope TP_A &amp; Associated Works</b>								Site Formation - Slope TP_A & Associated Works
<b>Achievement of KD-3(Stage 3) for Slope A</b>								Achievement of KD-3(Stage 3) for Slope A
TPA41830	Achievement of KD-3(Stage 3) for slope A							◆ Achievement of KD-3(Stage 3) for slope A
TPA41810	Remaining civil works and drainge works(After tunnel civil works construction)							Remaining civil works and drainge works(After tunnel civil works)
<b>Site Formation - Slope TP_B &amp; Associated Works</b>								
<b>Achievement of KD-3(Stage 3) for Slope B</b>								Achievement of KD-3(Stage 3) for Slope B
TPB41730	Achievement of KD-3(Stage 3) for slope B							Achievement of KD-3(Stage 3) for slope B
<b>Achievement of KD-8 (Section 5) for Slope B</b>								
TPB41760	Remaining works inculde landscape works and establishment works							
<b>Site Formation - Slope TP_E &amp; Associated Works</b>								
<b>Stage 3</b>								Stage 3
<b>Slope Feature - Slope TP_E Remaing Section and 5SE-D/C116</b>								Slope Feature - Slope TP_E Remaing Section and 5SE-D/C116
TPE62300	Excavation of Rock (7,920m3) for slope E2a							
TPE62700	Achievement of KD-3(Stage 3) for slope E							◆ Achievement of KD-3(Stage 3) for slope E
<b>Achievement of KD-8(Section 5) for Slope E</b>								
TPE65320	Remaining works inculde landscape works and establishment works							
<b>Site Formation - Slope Upgrading Works</b>								
<b>Stage 3 (Other Slope Features)</b>								
<b>Slope Feature - 5SE-D/C170</b>								
SFW10105	Raking Drain Construction							Raking Drain Construction
SFW10110	Drainge, U-channel (410m) and Handrailing							Drainge, U-channel (410m) and Handrailing
SFW10850	Achievement of KD-3(Stage 3)							Achievement of KD-3(Stage 3)
<b>Slope Feature - 5SE-D/C165</b>								
SFW10820	Drainge, U-channel (80m) and Handrailing							Drainge, U-channel (80m) and Handrailing
SFW10830	Hydroseeding and Erosion Control Mat							Hydroseeding and Erosion Control Mat
SFW10870	Achievement of KD-3(Stage 3)							Achievement of KD-3(Stage 3)
<b>Slope Feature - 5SE-D/C150</b>								
SFW10890	Achievement of KD-3(Stage 3)							◆ Achievement of KD-3(Stage 3)
<b>Slope Feature - 5SE-D/C152</b>								
SFW10250	Hydroseeding and Erosion Control Mat							Hydroseeding and Erosion Control Mat
SFW10910	Achievement of KD-3(Stage 3)							◆ Achievement of KD-3(Stage 3)
<b>Slope Feature - 5SE-D/C121</b>								
SFW10930	Achievement of KD-3(Stage 3)							◆ Achievement of KD-3(Stage 3)
<b>Slope Feature - 5SE-D/C122</b>								
SFW10950	Achievement of KD-3(Stage 3)							◆ Achievement of KD-3(Stage 3)
<b>Slope Feature - 5SE-D/C14</b>								
								Slope Feature - 5SE-D/C14

█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ▼ Summary

**CRBC - Kaden JV  
Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		

Activity ID	Activity Name	2017					2018							
		Oct	Nov	Dec	Jan	Feb	Jan	Feb	Mar	Apr				
SFW10350	Slope Modification													
SFW10360	Drainage, U-channel (60m) and Handrailing													
SFW10370	Hydroseeding and Erosion Control Mat													
SFW10970	Achievement of KD-3(Stage 3)													
<b>Slope Feature - 5SE-D/C149</b>														
SFW10380	Complete slope 5SE-D/C152													
SFW10990	Achievement of KD-3(Stage 3)													
<b>Slope Feature - 5SE-D/C115</b>														
SFW11010	Achievement of KD-3(Stage 3)													
<b>Slope Feature - 5SE-D/C18</b>														
SFW10460	Complete Bridge TD2 Decking													
SFW10470	Slope Modification													
SFW10480	Drainage, U-channel (60m) and Handrailing													
SFW10490	Hydroseeding and Erosion Control Mat													
SFW11030	Achievement of KD-3(Stage 3)													
<b>Slope Feature - 5SE-D/C21</b>														
SFW10550	Slope Modification													
SFW10560	Rock Mapping and Stabilization													
SFW11070	Achievement of KD-3(Stage 3)													
SFW10570	Hydroseeding and Erosion Control Mat													
<b>Slope Feature - 5SE-D/C171</b>														
SFW10610	Hydroseeding and Erosion Control Mat													
SFW10580	Complete slope 5SE-D/C21													
SFW11090	Achievement of KD-3(Stage 3)													
<b>Slope Feature - 5SE-D/C16</b>														
SFW10630	Slope Modification													
SFW10640	Rock Mapping and Stabilization													
<b>Slope Feature - 5SE-D/F60</b>														
SFW10670	Complete of Bridge TD2 decking													
SFW10680	Slope Modification													
SFW10690	Drainage, U-channel (360m) and Handrailing													
SFW11130	Achievement of KD-3(Stage 3)													
SFW10700	Hydroseeding and Erosion Control Mat													
<b>Slope Feature - 5SE-D/C158</b>														
SFW10710	Complete backfilling of RW_A													
SFW10720	Slope Modification													
<b>Slope Feature - 5SE-D/C17</b>														
SFW10750	Slope Modification													
SFW10760	Drainage, U-channel (180m) and Handrailing													

█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ⇨ Summary

**CRBC - Kaden JV  
Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		

Activity ID	Activity Name	2017		2018		
		Oct	Nov	Dec	Jan	Feb
SFW10770	Hydroseeding and Erosion Control Mat					Hydroseeding and
SFW11170	Achievement of KD-3(Stage 3)					◆ Achievement of KI
<b>Vehicular Underpass TN-01</b>						
<b>Stage 3</b>						
Road and Drainage Work, Utilities Works in Tunnel						
Road and Drainage Work, Utilities Works in Tunnel						
UDP34000	DN300	[Blue bar]				
UDP34010	DN100	[Blue bar]				
UDP34020	PCCW	[Blue bar]		[Red bar]		
UDP34030	Hutchison Global Communication Cable	[Blue bar]		[Red bar]		
UDP34040	Hong Kong Boaroband Network	[Blue bar]		[Red bar]		
UDP34050	Wharf T&T Duct and Joint Box	[Blue bar]		[Red bar]		
UDP34060	New World Telecom	[Blue bar]		[Red bar]		
UDP34070	Town Gas	[Blue bar]		[Red bar]		
UDP34080	Smartone Cable	[Blue bar]		[Red bar]		
UDP34090	HKC Cable	[Blue bar]		[Red bar]		
UDP34100	Pubic Lighting	[Blue bar]		[Red bar]		
UDP34110	CLP	[Blue bar]		[Red bar]		
UDP34130	Completion of this stage civil provision for E&M, TCSS	[Blue bar]		[Red bar]		
<b>Achievement of KD-8 (Section 5) for TN-01</b>						
UDP20640	Road works and Remaining works(Sundry Metalwork,etc)	[Blue bar]				
<b>Road and Drainage Work ,Utilities Works at for Lung Fu Road Roundabout</b>						
<b>Section 3</b>						
Utilites installation ,road and drainage works (TTA stage 1)						
LFR10440	TTA for Stage 2-0	[Blue bar]				
LFR10270	Filling Works	[Blue bar]		[Green bar]		
Utilites installation ,road and drainage works (TTA Stage 2-0)						
LFR10450	Drainage Work	[Blue bar]				
LFR10460	DN100,300,700,800	[Blue bar]				
LFR10470	PCCW	[Blue bar]		[Red bar]		
LFR10480	Hutchison Global Communication Cable	[Blue bar]		[Red bar]		
LFR10490	Hong Kong Boaroband Network	[Blue bar]		[Red bar]		
LFR10500	Wharf T&T Duct and Joint Box	[Blue bar]		[Red bar]		
LFR10510	New World Telecom	[Blue bar]		[Red bar]		
LFR10520	Town Gas	[Blue bar]		[Red bar]		
LFR10530	Smartone Cable	[Blue bar]		[Red bar]		
LFR10550	Pubic Lighting	[Blue bar]		[Red bar]		
LFR10560	CLP + CRD	[Blue bar]		[Red bar]		
LFR10570	TraxComm	[Blue bar]		[Red bar]		

█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ▼ Summary

**CRBC - Kaden JV**  
**Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		

Activity ID	Activity Name	2017					2018							
		Oct	Nov	Dec	Jan	Feb	Jan	Feb	Mar	Apr				
LFR10540	HKC Cable													
LFR10580	Completion of this stage civil provision for E&M, TCSS													
LFR10590	Irrigation System (m)													
LFR10600	Road Pavement													
LFR10610	TTA for Stage 2													
<b>Utilites installation ,road and drainage works (TTA Stage 2)</b>														
LFR10620	Filling Works													
LFR10680	PCCW													
LFR10630	Street Furniture													
LFR10660	Drainage Work													
<b>Road and Drainage Work ,Utilities Works at Lung Mun Road</b>														
<b>Lung Mun Road (Westbound)</b>														
<b>Ho Suen Street North</b>														
LMRWA1150	Irrigation System													
LMRWA1160	Road Pavement													
<b>Ho Suen Street South</b>														
LMRWA1190	DN200 CHK 0 - 50													
LMRWA1200	DN300 CHE 0 - 116													
LMRWA1210	DN100 CHG 0 - 112													
LMRWA1170	Drainage Work													
LMRWA1220	PCCW													
LMRWA1230	Hutchison Global Communication Cable													
LMRWA1240	Hong Kong Boaroband Network													
LMRWA1250	Wharf T&T Duct and Joint Box													
LMRWA1260	New World Telecom													
LMRWA1241	Street Furniture(Including eastbound)													
LMRWA1242	Sign Gantry(Including eastbound)													
LMRWA1270	Town Gas													
<b>Utilites installation ,road and drainage works for East Portal</b>														
EPA1000	Rock Cutting													
EPA1020	DN300 CHA 0 - 175&DN100													
EPA1030	Street furniture and sign gantry													
EPA1040	PCCW													
EPA1050	Hutchison Global Communication Cable													
EPA1060	Hong Kong Boaroband Network													
EPA1070	Wharf T&T Duct and Joint Box													
EPA1080	New World Telecom													
EPA1090	Town Gas													
EPA1100	Smartone Cable													

█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ▼ Summary

**CRBC - Kaden JV  
Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		

Activity ID	Activity Name	2017		2018		
		Oct	Nov	Dec	Jan	Feb
EPA1110	HKC Cable	[Blue bar]				[Red bar] HKC Cable
EPA1120	Pubic Lighting	[Blue bar]				[Red bar] P
EPA1130	CLP	[Blue bar]				[Red bar]
EPA1140	TraxComm	[Blue bar]				
<b>Utilites installation ,road and drainage works near portion D</b>						
TOLLA1030	PCCW	[Blue bar]		[Red bar]		PCCW
TOLLA1040	Hutchison Global Communication Cable	[Blue bar]		[Red bar]		Hutchison Global Communication Cable
TOLLA1050	Hong Kong Boaroband Network	[Blue bar]		[Red bar]		Hong Kong Boaroband Network
TOLLA1060	Wharf T&T Duct and Joint Box	[Blue bar]		[Red bar]		Wharf T&T Duct and Joint Box
TOLLA1070	New World Telecom	[Blue bar]		[Red bar]		New World Telecom
TOLLA1080	Town Gas	[Blue bar]			[Red bar]	Town Gas
TOLLA1090	Smartone Cable	[Blue bar]			[Red bar]	Smartone Cable
TOLLA1100	HKC Cable					[Green bar]
TOLLA1092	Street Furniture					[Red bar]
TOLLA1094	Sign Gantry					[Red bar]
<b>Sewage, Irrigation and Road&amp; Drainage Works</b>						
SAII0020	Sewage, irrigation and road&drainage works - RW_B-north side	[Blue bar]				[Green bar]
SAII0060	Sewage, irrigation and road&drainage works -G2-north side	[Blue bar]				
SAII0070	Sewage, irrigation and road&drainage works- G2-south side	[Blue bar]				
SAII0030	Sewage, irrigation and road&drainage works - RW_B-south side	[Blue bar]				
SAII0040	Sewage, irrigation and road&drainage works -G1&H1-north side	[Blue bar]				
SAII0050	Sewage, irrigation and road&drainage works - G1&H1-south side	[Blue bar]				
<b>Achievement of Key Dates</b>						
AK10300	Achievement of KD-3(Stage 3) for slope B					◆ Achievement of KD-3(Stage 3) for slope B
AK10330	Achievement of KD-8(Section 5) for slope C					◆ Achievement of KD-8(Section 5) for slope C
AK10320	Achievement of KD-3(Stage 3) for slope C					◆ Achievement of KD-3(Stage 3) for slope C
AK10250	Achievement of KD-3(stage 3) for TP_F					◆ Achievement of KD-3(stage 3) for TP_F
AK10060	Achievement of KD-1(Stage 1) for RW_B					◆ Achievement of KD-1(Stage 1) for RW_B
AK10210	Achievement of KD-3(Stage 3) for RW_A					◆ Achievement of KD-3(Stage 3) for RW_A
AK10280	Achievement of KD-3(Stage 3) for slope A					◆ Achievement of KD-3(Stage 3) for slope A
AK10020	Achievement of KD-1(Stage 1) for TD2					◆ Achievement of KD-1(Stage 1) for TD2
AK10000	Achievement of KD-1( stage 1) for TD1					◆ Achievement of KD-1( stage 1) for TD1
AK10455	Achievement of KD-3(Stage 3) for Road and draiange Works under TD1					◆ Achievement of K


█ Remaining Level of Effort    █ Critical Remaining Work  
█ Actual Work    ◆ Milestone  
█ Remaining Work    ▬ Summary

**CRBC - Kaden JV  
Three-Month Rolling Programme**

Date	Revision	Checked	Approved
28-11-17	4		

## **Appendix E**

### **Monitoring Locations / Sensitive Receivers for the Contract**

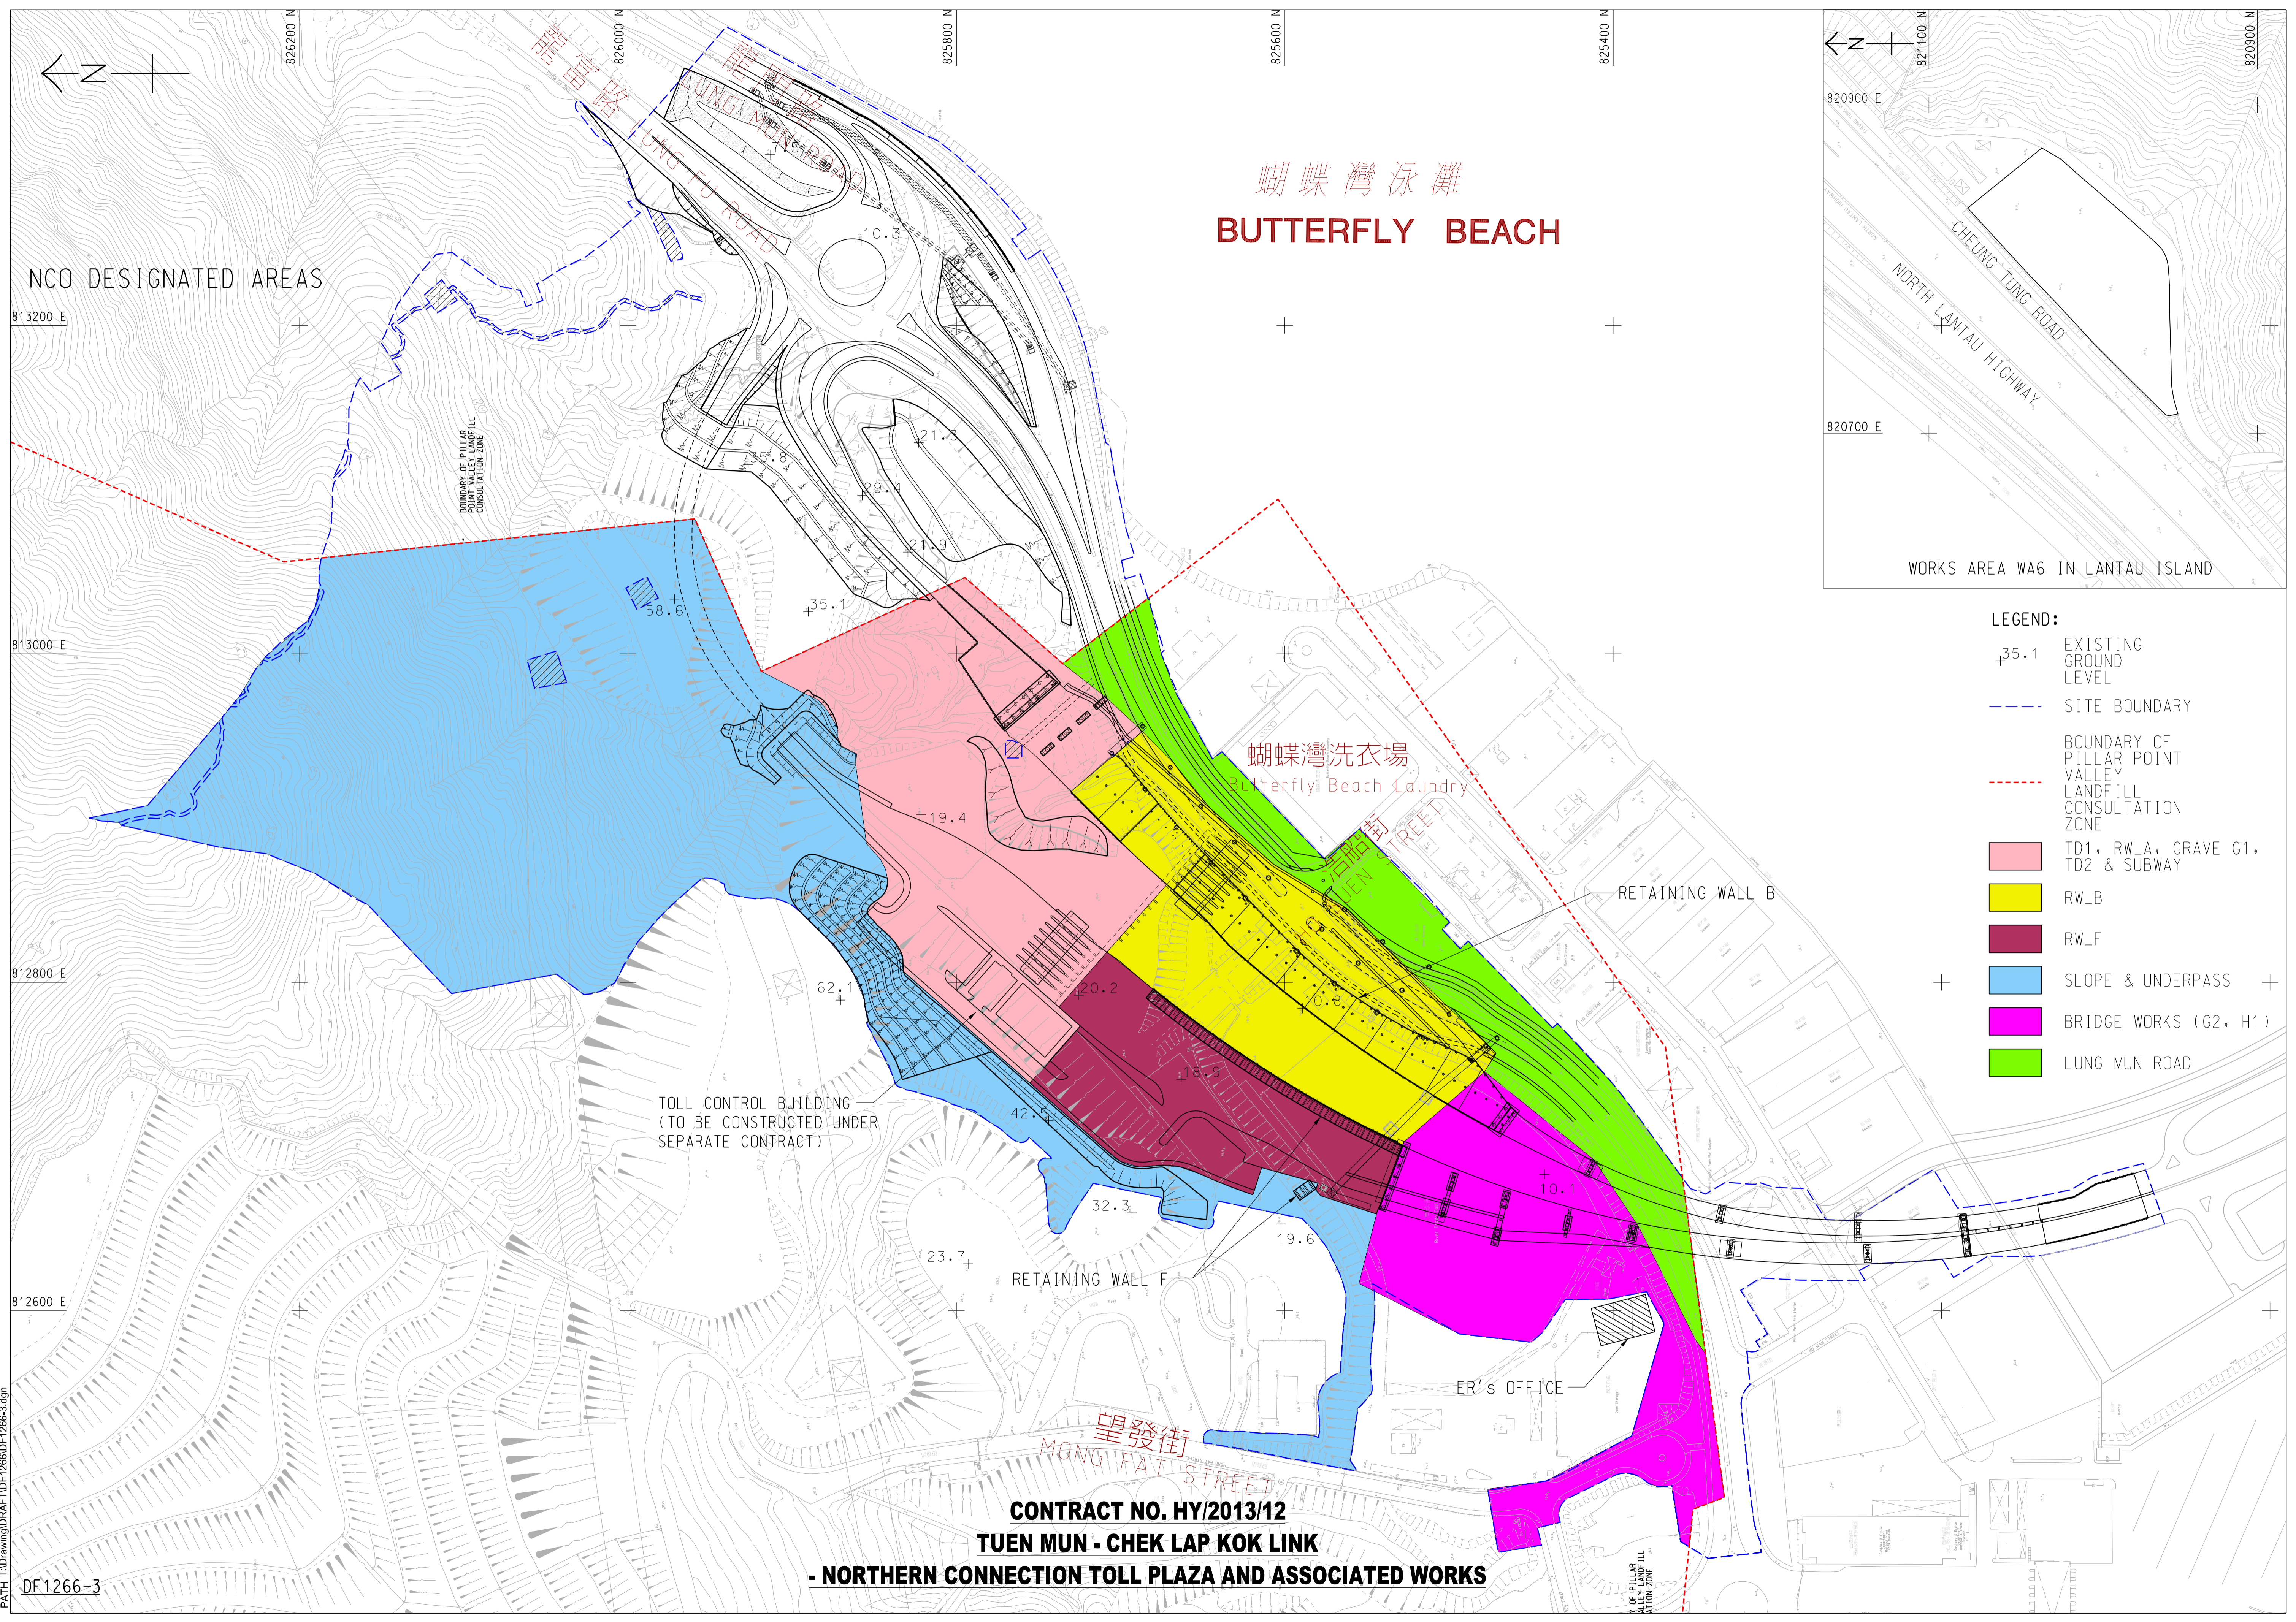

蝴蝶灣泳灘  
**BUTTERFLY BEACH**

NCO DESIGNATED AREAS

WORKS AREA WA6 IN LANTAU ISLAND

- LEGEND:**
- +35.1 EXISTING GROUND LEVEL
  - - - SITE BOUNDARY
  - - - BOUNDARY OF PILLAR POINT VALLEY LANDFILL CONSULTATION ZONE
  - TD1, RW\_A, GRAVE G1, TD2 & SUBWAY
  - RW\_B
  - RW\_F
  - SLOPE & UNDERPASS
  - BRIDGE WORKS (G2, H1)
  - LUNG MUN ROAD

TOLL CONTROL BUILDING  
 (TO BE CONSTRUCTED UNDER  
 SEPARATE CONTRACT)

蝴蝶灣洗衣場  
 Butterfly Beach Laundry

RETAINING WALL B

RETAINING WALL F

ER'S OFFICE


望發街  
 MONG FAT STREET

**CONTRACT NO. HY/2013/12**  
**TUEN MUN - CHEK LAP KOK LINK**  
**- NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS**

Plot File: byr\_rasc01  
 10/Mar/17 4:32:51 PM  
 PATH: T:\Drawing\DRAF\1DF1266\DF1266-3.dgn

DF1266-3



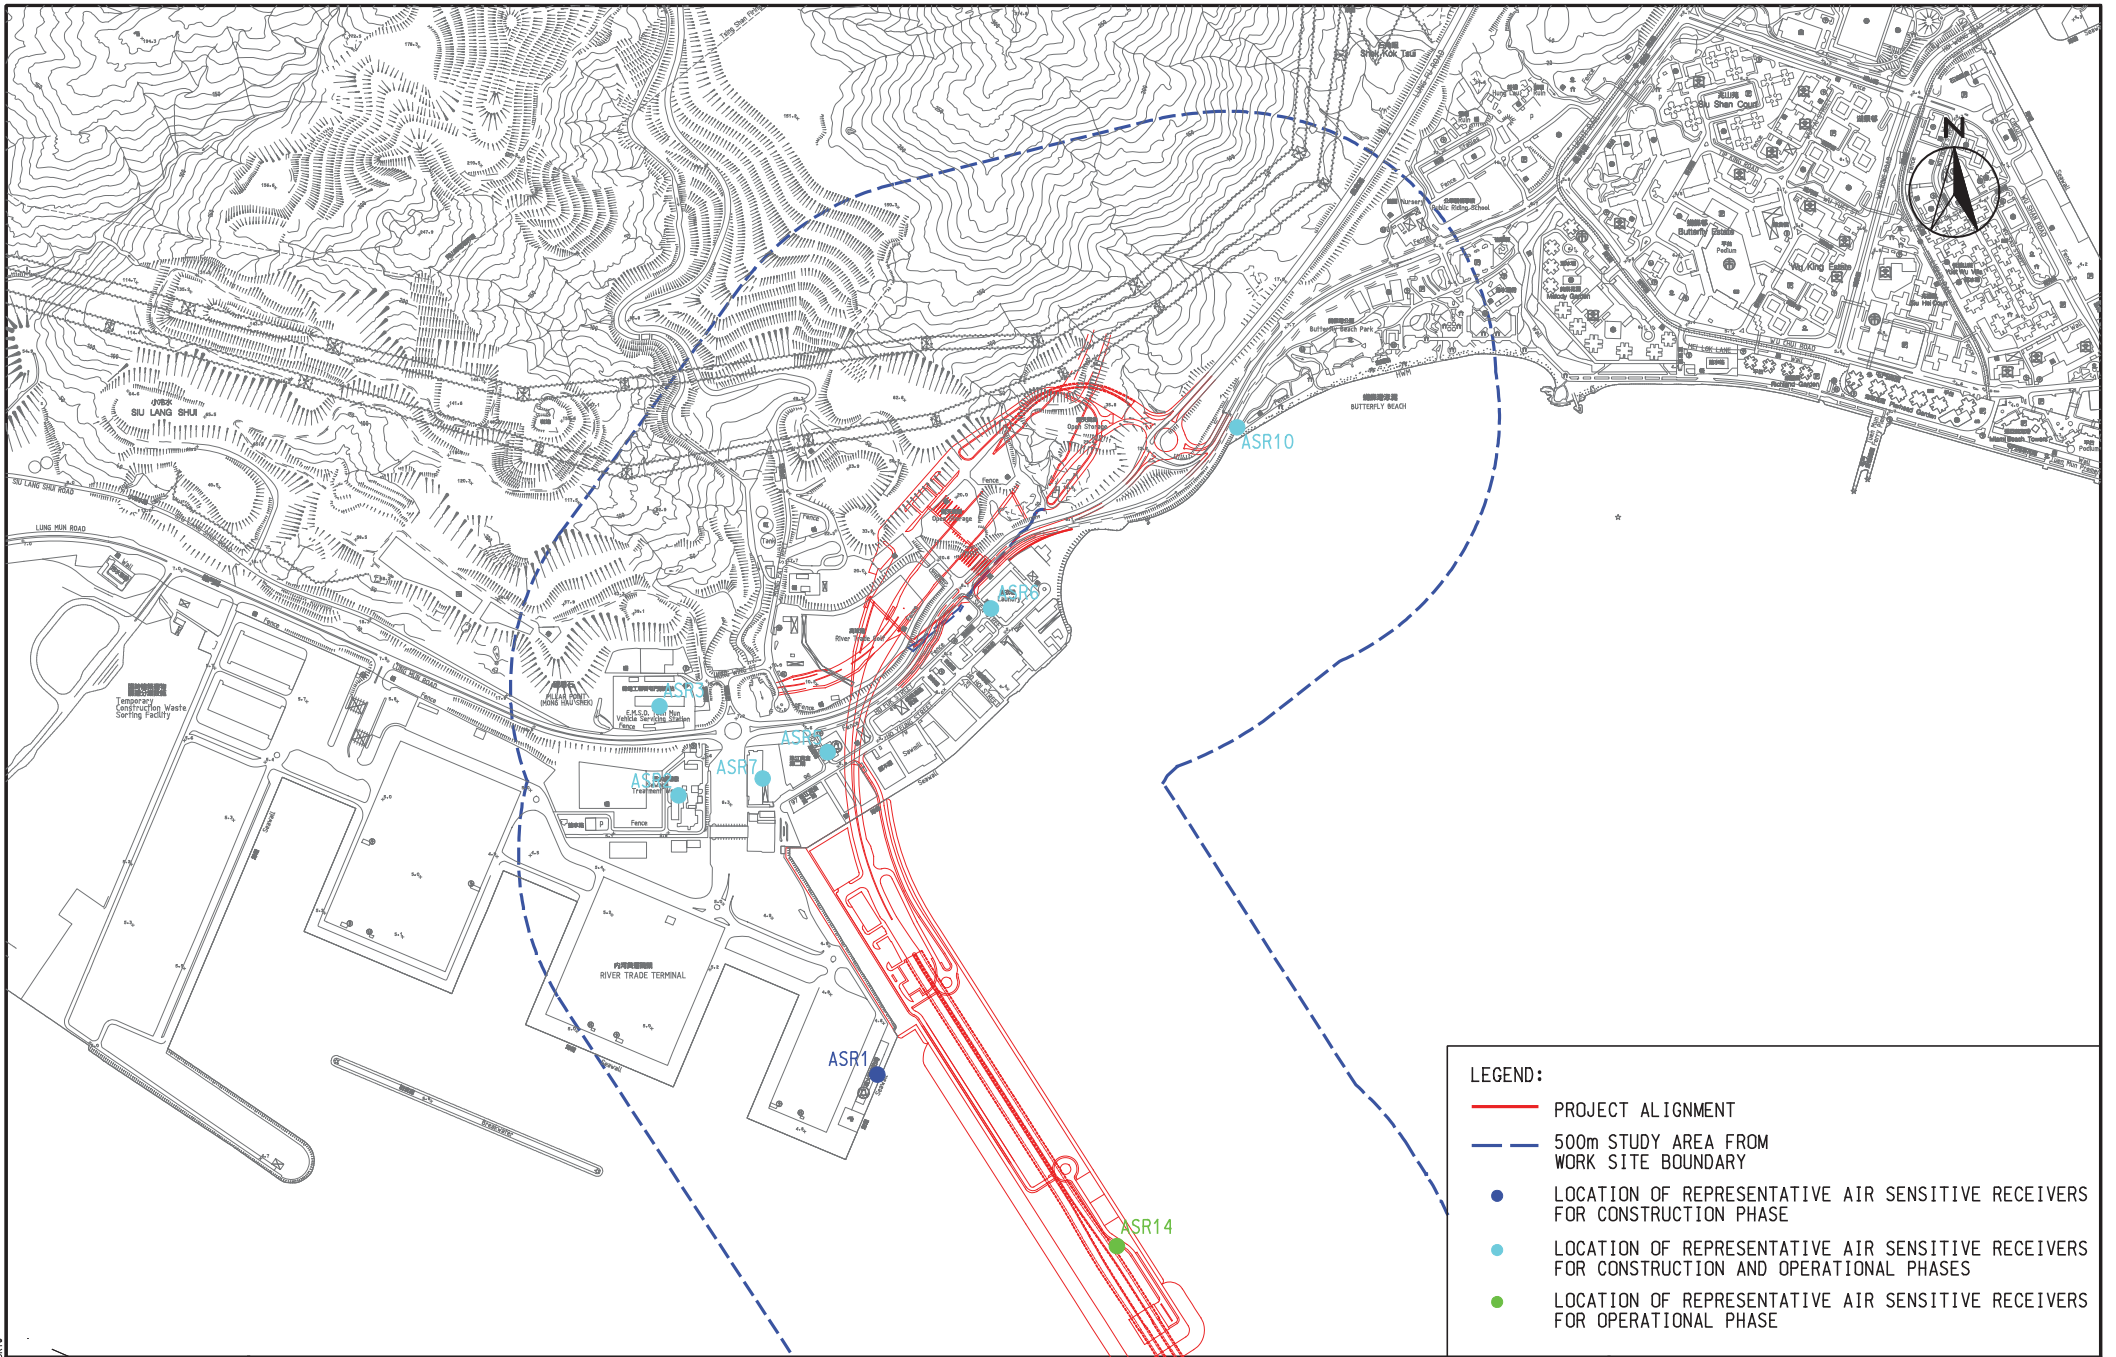


**LEGEND:**


- PROJECT ALIGNMENT
- - - 500m STUDY AREA FROM WORK SITE BOUNDARY
- LOCATION OF REPRESENTATIVE AIR SENSITIVE RECEIVERS FOR CONSTRUCTION PHASE
- LOCATION OF REPRESENTATIVE AIR SENSITIVE RECEIVERS FOR CONSTRUCTION AND OPERATIONAL PHASES
- LOCATION OF REPRESENTATIVE AIR SENSITIVE RECEIVERS FOR OPERATIONAL PHASE

AGREEMENT NO. CE 52/2007(HY)  
 TUEN MUN - CHEK LAP KOK LINK - INVESTIGATION  
**REPRESENTATIVE AIR SENSITIVE RECEIVERS**



SCALE	1 : 10 000	DATE	
-------	------------	------	--

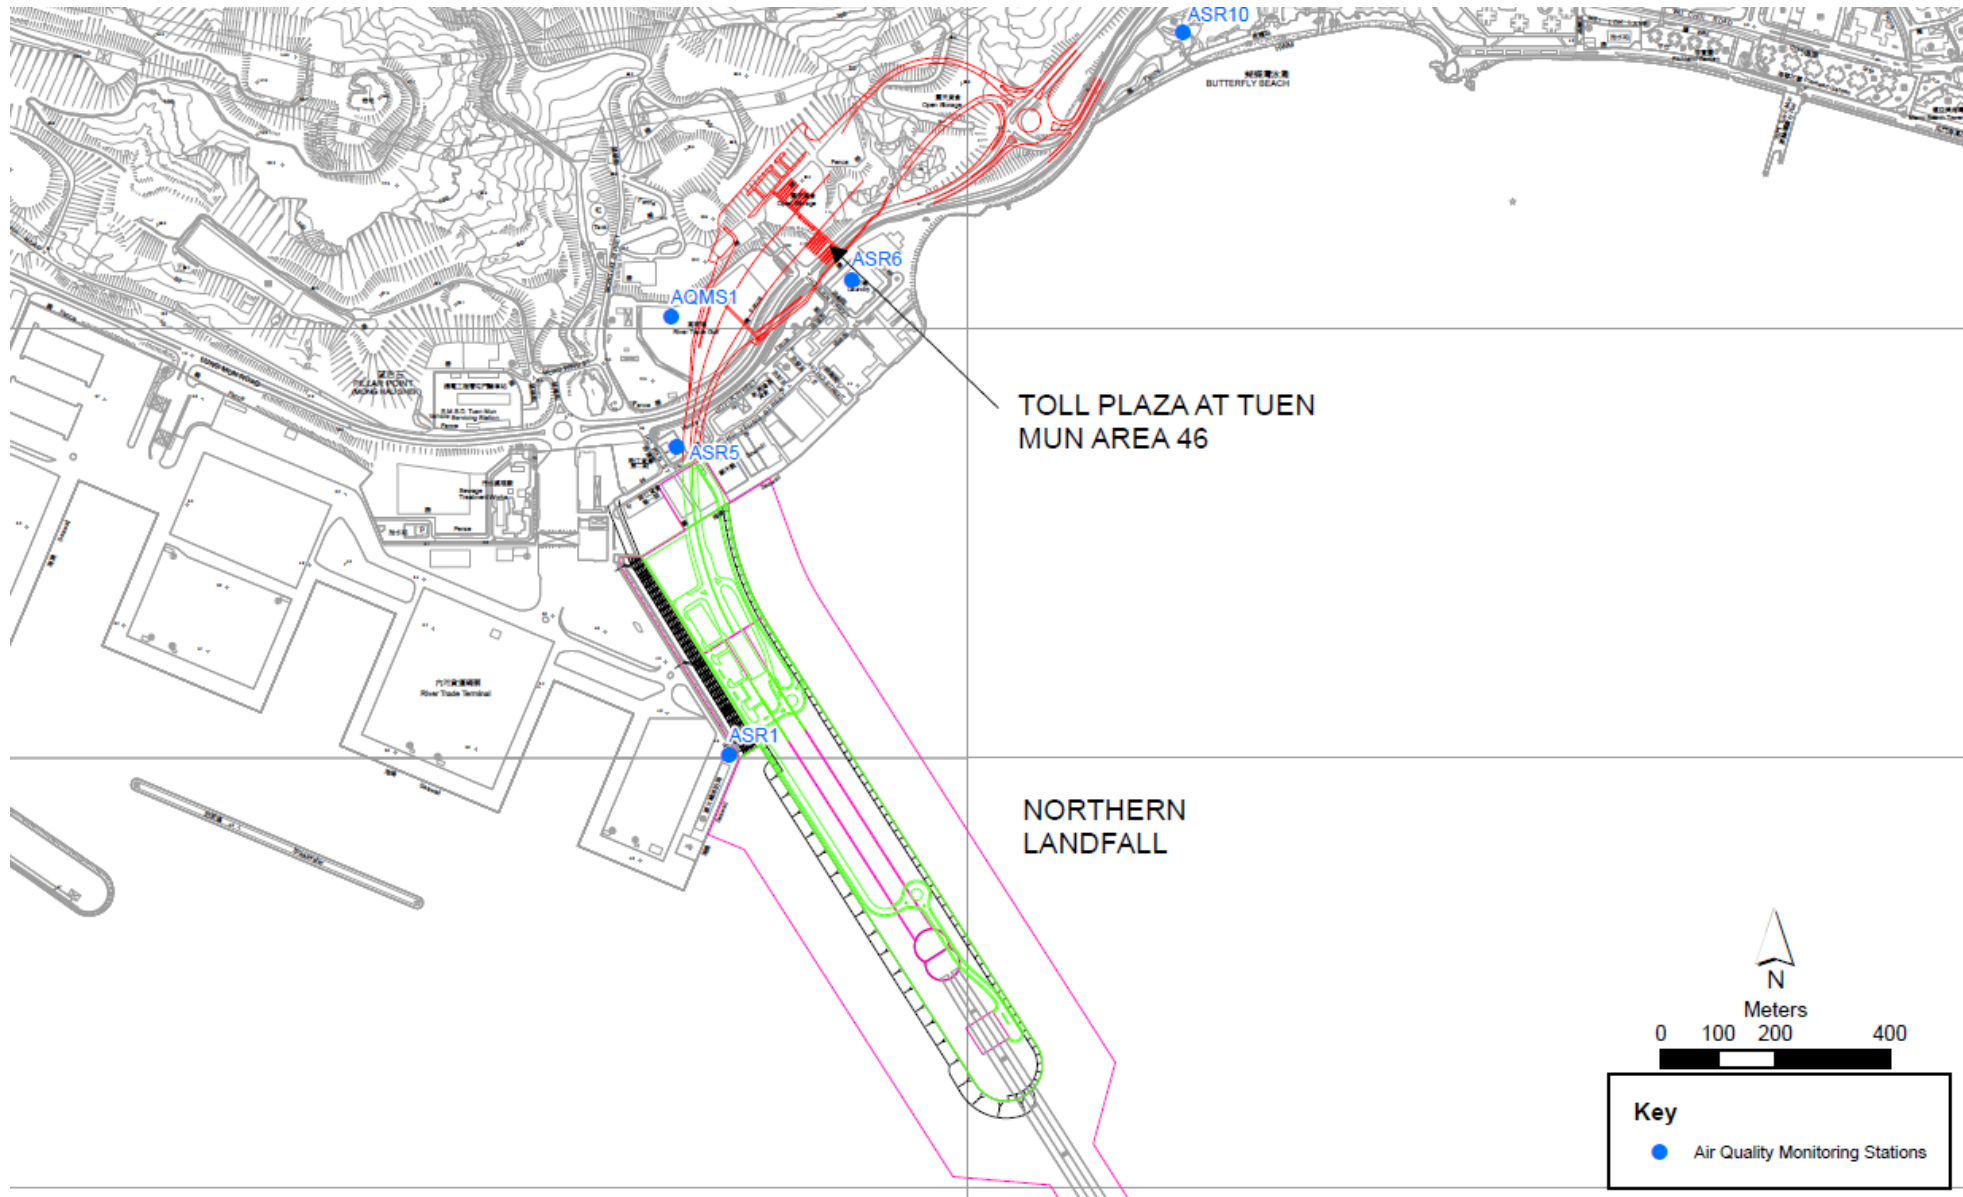

**Air Quality Monitoring Location**

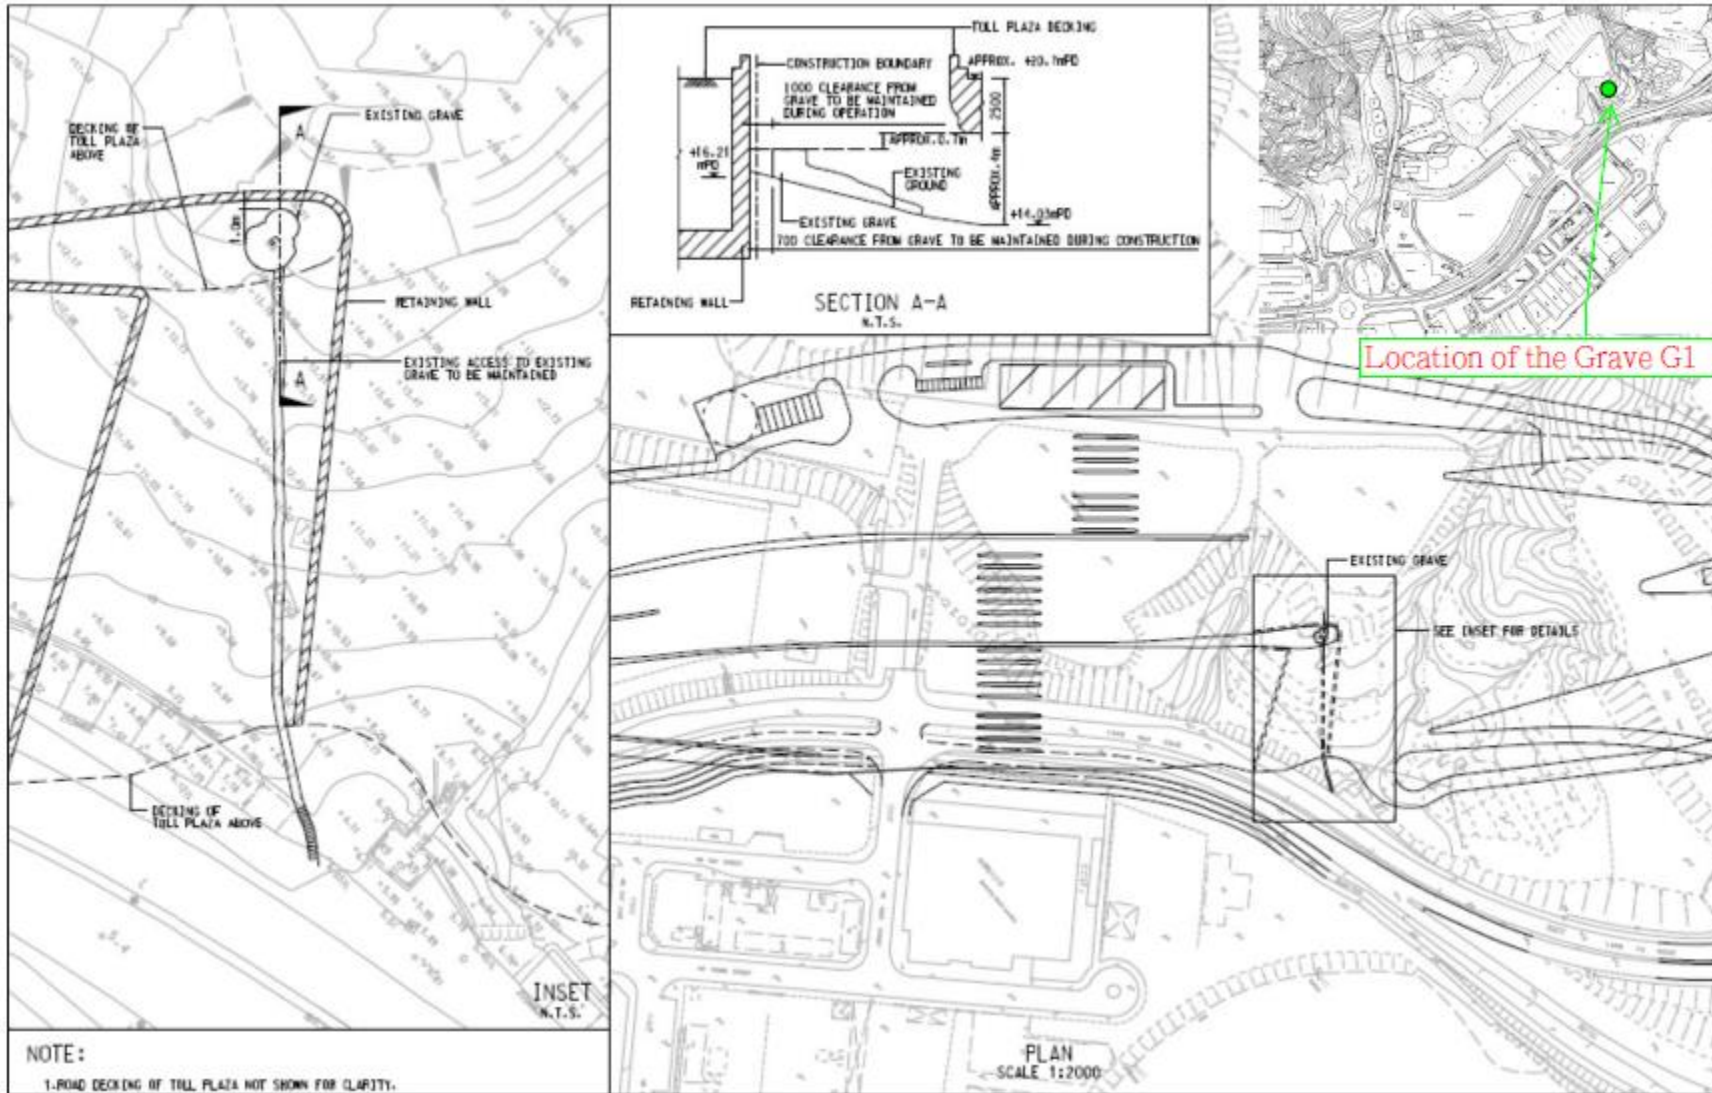

**Location of the Grave G1**

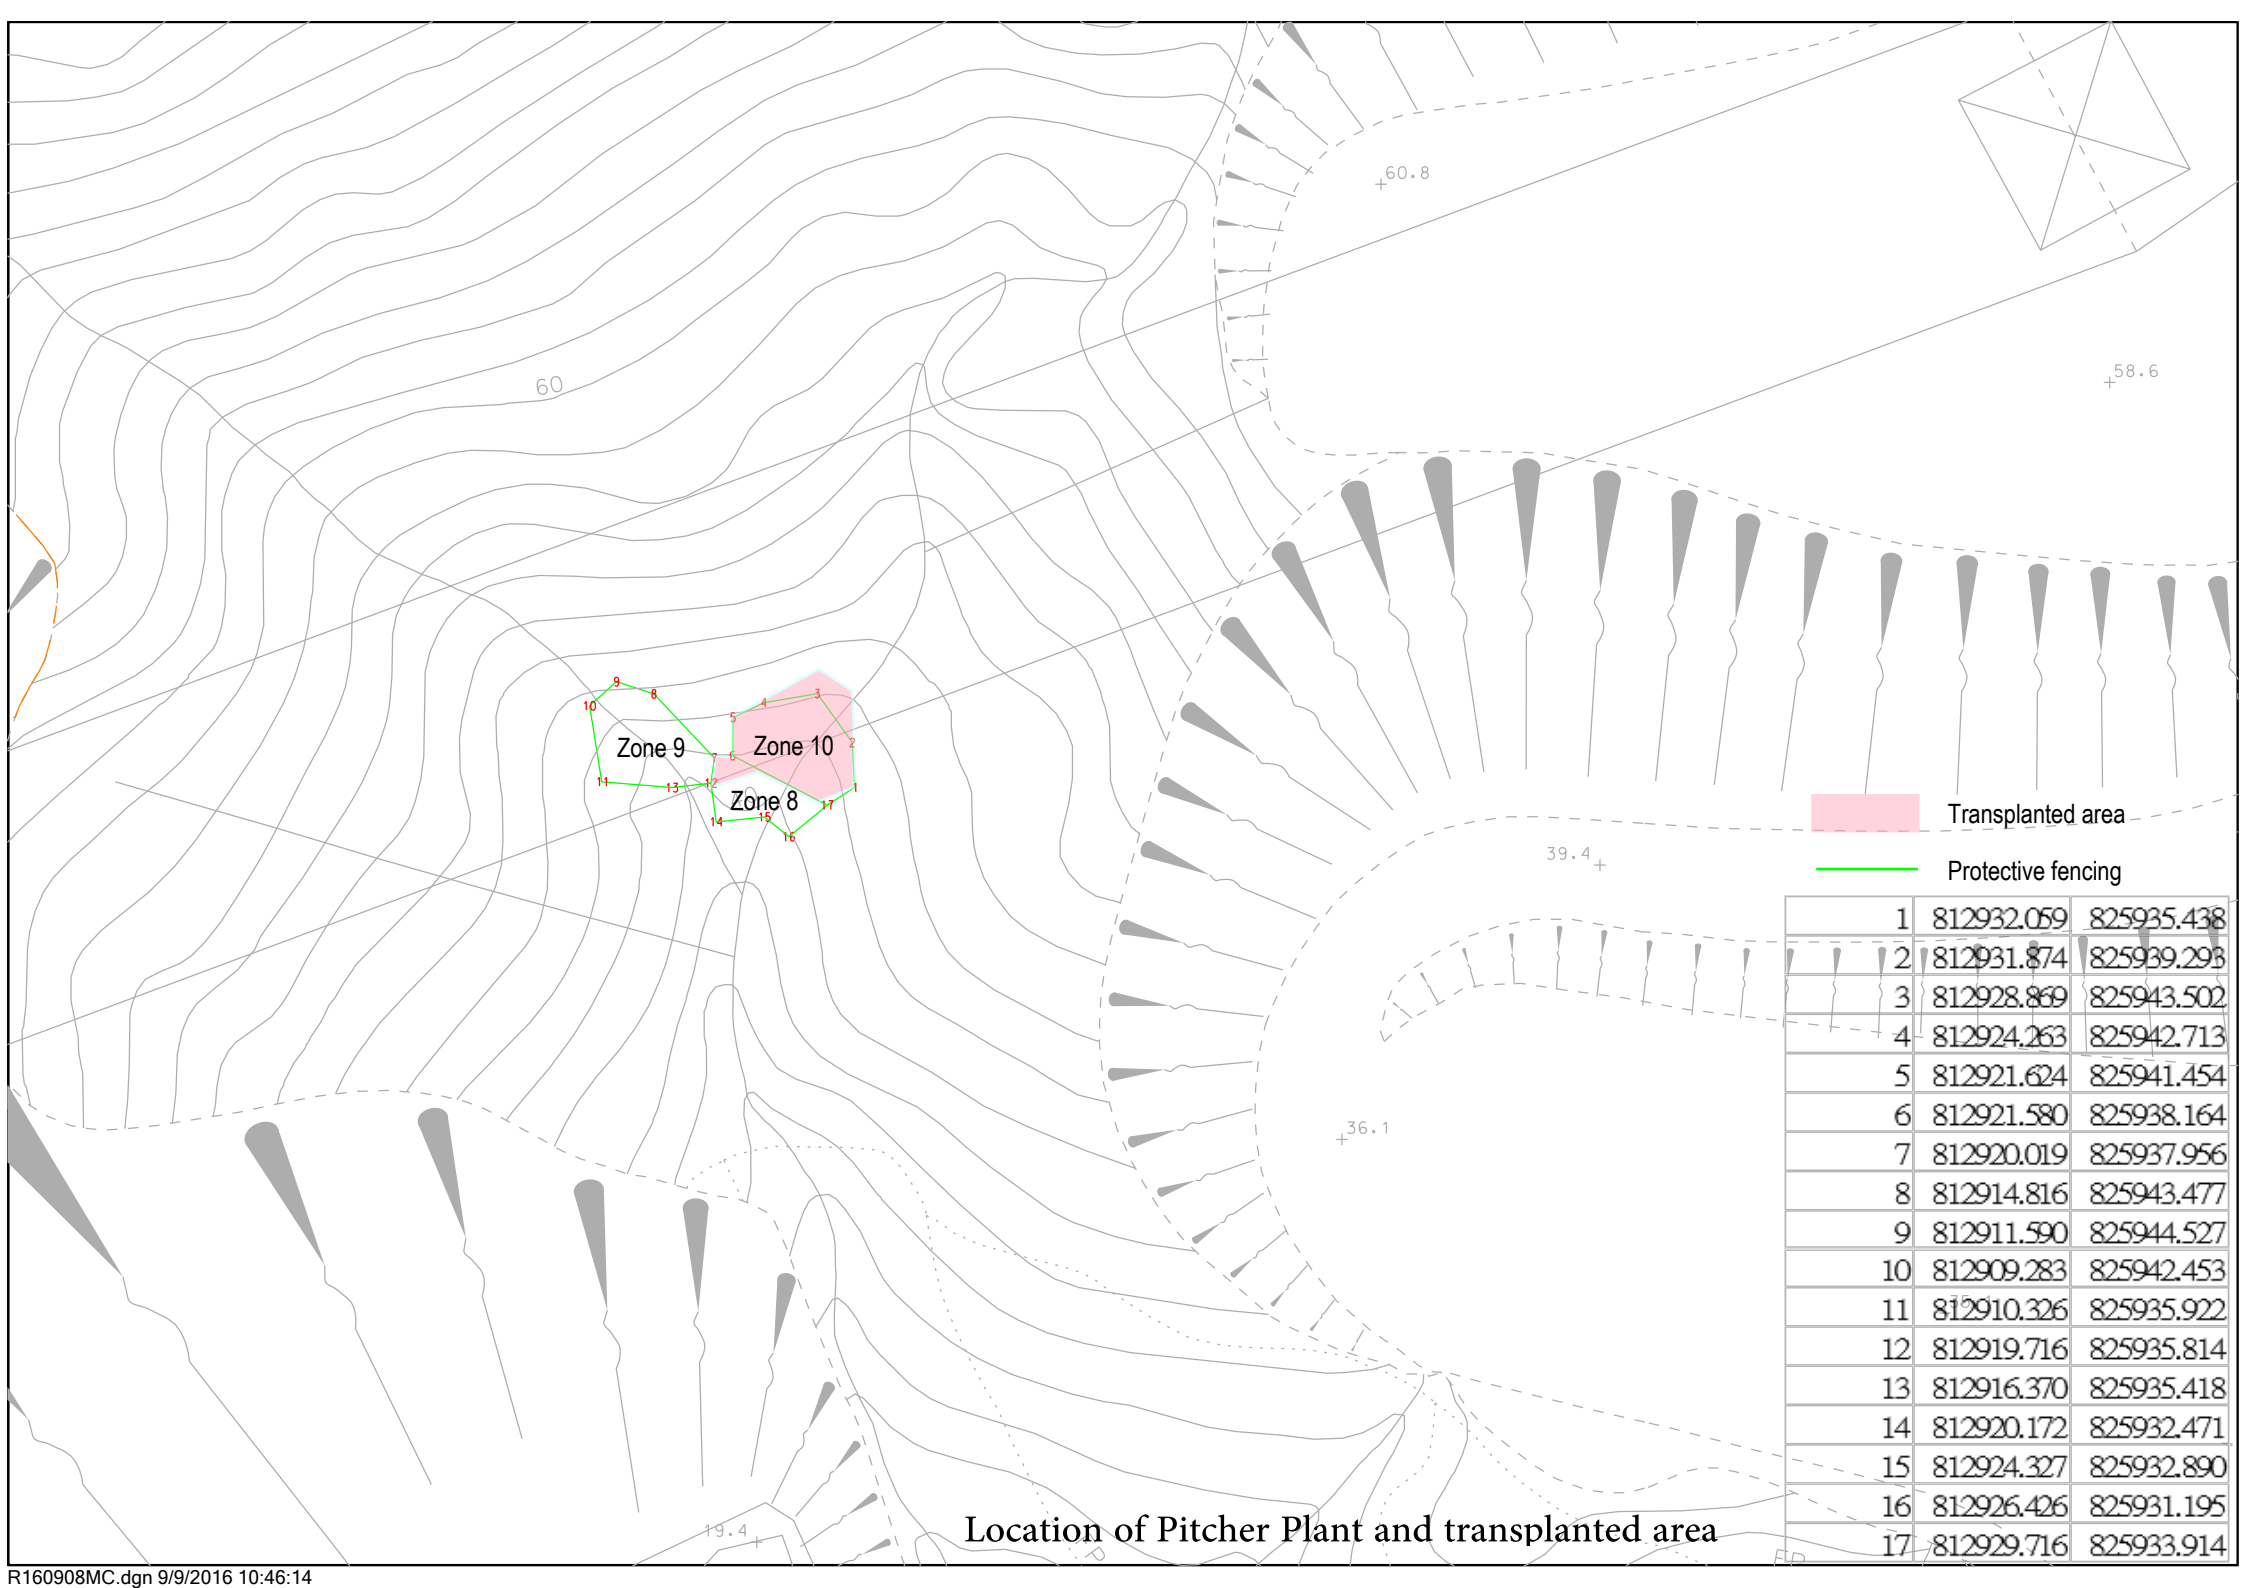

Transplanted area  
 Protective fencing

1	812932.059	825935.438
2	812931.874	825939.293
3	812928.869	825943.502
4	812924.263	825942.713
5	812921.624	825941.454
6	812921.580	825938.164
7	812920.019	825937.956
8	812914.816	825943.477
9	812911.590	825944.527
10	812909.283	825942.453
11	812910.326	825935.922
12	812919.716	825935.814
13	812916.370	825935.418
14	812920.172	825932.471
15	812924.327	825932.890
16	812926.426	825931.195
17	812929.716	825933.914

Location of Pitcher Plant and transplanted area

## **Appendix F**

### **Event and Action Plan**

### Event and Action Plan for Air Quality

EVENT	ACTION			
	ET <sup>(1)</sup>	IEC <sup>(1)</sup>	SOR <sup>(1)</sup>	Contractor(s)
<b>Action Level</b>				
Exceedance recorded	<ol style="list-style-type: none"> <li>1 Identify the source.</li> <li>2 Repeat measurements to confirm findings. If two consecutive measurements exceed Action Level, the exceedance is then confirmed.</li> <li>3 Inform the IEC and the SOR</li> <li>4 Investigate the cause of exceedance and check Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>5 If the exceedance is confirmed to be Project related after investigation, increase monitoring frequency to daily.</li> <li>6 Discuss with the IEC and the Contractor on remedial actions required.</li> <li>7 If exceedance continues, arrange meeting with the IEC and the SOR.</li> <li>8 If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1 Check monitoring data submitted by the ET.</li> <li>2 Check the Contractor's working method.</li> <li>3 If the exceedance is confirmed to be Project related after investigation, discuss with the ET and the Contractor on possible remedial measures.</li> <li>4 Advise the SOR on the effectiveness of the proposed remedial measures.</li> <li>5 Supervisor implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1 Confirm receipt of notification of failure in writing.</li> <li>2 Notify the Contractor.</li> <li>3 Ensure remedial measures properly implemented.</li> </ol>	<ol style="list-style-type: none"> <li>1 Rectify any unacceptable practice.</li> <li>2 Amend working methods if appropriate</li> <li>3 If the exceedance is confirmed to be Project related, submit proposals for remedial actions to IEC within 3 working days of notification</li> <li>4 Implement the agreed proposals</li> <li>5 Amend proposal if appropriate.</li> </ol>
<b>Limit Level</b>				
Exceedance recorded	<ol style="list-style-type: none"> <li>1. Identify the source.</li> <li>2. Repeat measurement to confirm finding. If two consecutive measurements exceed Limit Level, the exceedance is then confirmed.</li> <li>3. Inform the IEC, the SOR, the DEP and the Contractor.</li> <li>4. Investigate the cause of exceedance and check Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>5. If the exceedance is confirmed to be Project related after investigation, increase monitoring frequency to daily.</li> <li>6. Carry out analysis of the Contractor's working procedures to determine possible mitigation to be implemented.</li> <li>7. Arrange meeting with the IEC and the SOR to discuss the remedial actions to be taken.</li> <li>8. Assess effectiveness of the Contractor's remedial actions and keep the IEC, the DEP and the SOR informed of the results.</li> <li>9. If exceedance stops, cease additional monitoring.</li> </ol>	<ol style="list-style-type: none"> <li>1 Check monitoring data submitted by the ET.</li> <li>2 Check Contractor's working method.</li> <li>3 If the exceedance is confirmed to be Project related after investigation, discuss with the ET and the Contractor on possible remedial measures.</li> <li>4 Advise the SOR on the effectiveness of the proposed remedial measures.</li> <li>5 Supervisor implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing.</li> <li>2. Notify the Contractor.</li> <li>3. If the exceedance is confirmed to be Project related after investigation, in consultation with the IEC, agree with the Contractor on the remedial measures to be implemented.</li> <li>4. Ensure remedial measures are properly implemented.</li> <li>5. If exceedance continues, consider what activity of the work is responsible and instruct the Contractor to stop that activity of work until the exceedance is abated.</li> </ol>	<ol style="list-style-type: none"> <li>1 Take immediate action to avoid further exceedance.</li> <li>2 If the exceedance is confirmed to be Project related after investigation, submit proposals for remedial actions to IEC within 3 working days of notification.</li> <li>3 Implement the agreed proposals.</li> <li>4 Amend proposal if appropriate.</li> <li>5 Stop the relevant activity of works as determined by the SOR until the exceedance is abated.</li> </ol>

### Event and Action Plan for Landscape and Visual Impact

EVENT ACTION LEVEL	ACTION			
	ET	IEC	ER	Contractor
Design Check	<ul style="list-style-type: none"> <li>Check final design conforms to the requirements of EP and prepare report.</li> </ul>	<ul style="list-style-type: none"> <li>Check report.</li> <li>Recommend remedial design if necessary</li> </ul>	<ul style="list-style-type: none"> <li>Undertake remedial design if necessary</li> </ul>	
Non- conformity on one occasion	<ul style="list-style-type: none"> <li>Identify Source</li> <li>Inform IEC and ER</li> <li>Discuss remedial actions with IEC, ER and Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> </ul>	<ul style="list-style-type: none"> <li>Check report</li> <li>Check Contractor's working method</li> <li>Discuss with ET and Contractor on possible remedial measures</li> <li>Advise ER on effectiveness of proposed remedial measures.</li> <li>Check implementation of remedial measures</li> </ul>	<ul style="list-style-type: none"> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ul>	<ul style="list-style-type: none"> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>
Repeated Non-conformity	<ul style="list-style-type: none"> <li>Identify Source</li> <li>Inform IEC and ER</li> <li>Increase monitoring frequency</li> <li>Discuss remedial actions with IEC, ER and Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> <li>If nonconformity stops, cease additional monitoring</li> </ul>	<ul style="list-style-type: none"> <li>Check monitoring report</li> <li>Check Contractor's working method</li> <li>Discuss with ET and Contractor on possible remedial measures</li> <li>Advise ER on effectiveness of proposed remedial measures</li> <li>Supervise implementation of remedial measures</li> </ul>	<ul style="list-style-type: none"> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> </ul>	<ul style="list-style-type: none"> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>

**Event / Action Plan for Cultural Heritage**

<b>Action Level</b>	<b>ET</b>	<b>IC (E)</b>	<b>ER</b>	<b>Contractor</b>
Non- conformity on one occasion	<ol style="list-style-type: none"> <li>1. Identify Source</li> <li>2. Inform the IEC and the ER</li> <li>3. Discuss remedial actions with the IEC, the ER and the Contractor</li> <li>4. Monitor remedial actions until rectification has been completed</li> </ol>	<ol style="list-style-type: none"> <li>1. Check report</li> <li>2. Check the Contractor's working method</li> <li>3. Discuss with the ET and the Contractor on possible remedial measures</li> <li>4. Advise the ER on effectiveness of proposed remedial measures.</li> <li>5. Check implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify Contractor</li> <li>2. Ensure remedial measures are properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Amend working methods</li> <li>2. Rectify damage and undertake any necessary replacement</li> </ol>
Repeated Non-conformity	<ol style="list-style-type: none"> <li>1. Identify Source</li> <li>2. Inform the IC(E) and the ER</li> <li>3. Increase monitoring frequency</li> <li>4. Discuss remedial actions with the IC(E), the ER and the Contractor</li> <li>5. Monitor remedial actions until</li> <li>6. rectification has been completed</li> <li>7. If exceedance stops, cease additional monitoring</li> </ol>	<ol style="list-style-type: none"> <li>1. Check monitoring report</li> <li>2. Check the Contractor's working method</li> <li>3. Discuss with the ES and the Contractor on possible remedial measures</li> <li>4. Advise the ER on effectiveness of proposed remedial measures</li> <li>5. Supervise implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>1. Notify the Contractor</li> <li>2. Ensure remedial measures are properly implemented</li> </ol>	<ol style="list-style-type: none"> <li>1. Amend working methods</li> <li>2. Rectify damage and undertake any necessary replacement</li> </ol>

*Note:*

ET – Environmental Specialist, IEC – Independent Environmental Checker, ER – Engineer’s Representative



**Event / Action Plan for General Ecology**

<b>Action Level</b>	<b>ET</b>	<b>IEC</b>	<b>ER</b>	<b>Contractor</b>
Non-conformity on one occasion	<ul style="list-style-type: none"> <li>Identify Source</li> <li>Inform the IEC and the ER</li> <li>Discuss remedial actions with the IEC, the ER and the Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> </ul>	<ul style="list-style-type: none"> <li>Check report</li> <li>Check the Contractor's working method</li> <li>Discuss with the ET and the Contractor on possible remedial measures</li> <li>Advise the ER on effectiveness of proposed remedial measures.</li> <li>Check implementation of remedial measures.</li> </ul>	<ul style="list-style-type: none"> <li>Notify Contractor</li> <li>Ensure remedial measures are properly implemented</li> <li>Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the works in the case of a serious nonconformity until situation rectified.</li> </ul>	<ul style="list-style-type: none"> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>
Repeated Non conformity	<ul style="list-style-type: none"> <li>Identify Source</li> <li>Inform the IC(E) and the ER</li> <li>Increase monitoring frequency</li> <li>Discuss remedial actions with the IC(E), the ER and the Contractor</li> <li>Monitor remedial actions until rectification has been completed</li> <li>If exceedance stops, cease additional monitoring</li> </ul>	<ul style="list-style-type: none"> <li>Check monitoring report</li> <li>Check the Contractor's working method</li> <li>Discuss with the ES and the Contractor on possible remedial measures</li> <li>Advise the ER on effectiveness of proposed remedial measures</li> <li>Supervise implementation of remedial measures</li> </ul>	<ul style="list-style-type: none"> <li>Notify the Contractor</li> <li>Ensure remedial measures are properly implemented</li> <li>Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the works in the case of a serious nonconformity until situation rectified.</li> </ul>	<ul style="list-style-type: none"> <li>Amend working methods</li> <li>Rectify damage and undertake any necessary replacement</li> </ul>

Note:

ET – Environmental Specialist, IC(E) – Independent Checker (Environmental), ER – Engineer’s Representative

**Actions in the Event of Landfill Gas being Detected in Excavation / Confined Area**

Parameter	Measurement	Action
Oxygen	< 19%	- Ventilate to restore oxygen to > 19%
	< 18%	- Stop work - Evacuate personnel / prohibit entry - Increase ventilation to restore to > 19%
Methane	> 10% LEL (> 0.5% v/v)	- Prohibit hot work - Ventilate to restore methane to < 10% LEL
	> 20% LEL (>1% v/v)	- Stop work - Evacuate personnel / prohibit entry - Increase ventilation to restore to < 10%
Carbon Dioxide	> 0.5%	- Ventilate to restore oxygen to < 0.5%
	> 1.5%	- Stop work - Evacuate personnel / prohibit entry - Increase ventilation to restore to < 0.5%

## **Appendix G**

### **Monitoring Schedule**

**Impact Monitoring Schedule for November 2017**

Date		Landfill Gas Monitoring	Landscape and Visual Monitoring
Wed	1-November-17	✓	
Thu	2-November-17	✓	
Fri	3-November-17	✓	✓
Sat	4-November-17	✓	
Sun	5-November-17		
Mon	6-November-17	✓	
Tue	7-November-17	✓	
Wed	8-November-17	✓	
Thu	9-November-17	✓	
Fri	10-November-17	✓	✓
Sat	11-November-17	✓	
Sun	12-November-17		
Mon	13-November-17	✓	
Tue	14-November-17	✓	
Wed	15-November-17	✓	
Thu	16-November-17	✓	
Fri	17-November-17	✓	✓
Sat	18-November-17	✓	
Sun	19-November-17		
Mon	20-November-17	✓	
Tue	21-November-17	✓	
Wed	22-November-17	✓	
Thu	23-November-17	✓	
Fri	24-November-17	✓	✓
Sat	25-November-17	✓	
Sun	26-November-17		
Mon	27-November-17	✓	
Tue	28-November-17	✓	
Wed	29-November-17	✓	
Thu	30-November-17	✓	

✓	Monitoring Day
	Sunday or Public Holiday

**Impact Monitoring Schedule for December 2017**

Date		Landfill Gas Monitoring	Landscape and Visual Monitoring
Fri	1-December-17	✓	✓
Sat	2-December-17	✓	
Sun	3-December-17		
Mon	4-December-17	✓	
Tue	5-December-17	✓	
Wed	6-December-17	✓	
Thu	7-December-17	✓	
Fri	8-December-17	✓	✓
Sat	9-December-17	✓	
Sun	10-December-17		
Mon	11-December-17	✓	
Tue	12-December-17	✓	
Wed	13-December-17	✓	
Thu	14-December-17	✓	
Fri	15-December-17	✓	✓
Sat	16-December-17	✓	
Sun	17-December-17		
Mon	18-December-17	✓	
Tue	19-December-17	✓	
Wed	20-December-17	✓	
Thu	21-December-17	✓	
Fri	22-December-17	✓	✓
Sat	23-December-17	✓	
Sun	24-December-17		
Mon	25-December-17		
Tue	26-December-17		
Wed	27-December-17	✓	
Thu	28-December-17	✓	
Fri	29-December-17	✓	✓
Sat	30-December-17	✓	
Sun	31-December-17		

✓	Monitoring Day
	Sunday or Public Holiday

## **Appendix H**

### **Calibration Certificates of Monitoring Equipment**

# CERTIFICATION OF CALIBRATION

Date Of Calibration: 20-Jun-2017 Certificate Number: G503226\_2/18640



# Geotech

ISSUED BY: GEOTECHNICAL INSTRUMENTS (UK) LTD

**Customer:** Fugro Geotechnical Services Ltd  
Units 6, 8-11 10/F Worldwide Industrial Centre 43-47 Shan Mei Street  
Fo Tan Sha Tin, N.T. HONG KONG

**Description:** Gas Analyser

**Model:** BIOGAS 5000

**Serial Number:** G503226

## UKAS Accredited results:

Results after adjustment :

Methane (CH <sub>4</sub> )		
Certified Gas (%)	Instrument Reading (%)	Uncertainty (%)
5.1	4.9	0.41
15.0	14.8	0.64
50.0	49.4	0.94

Carbon Dioxide (CO <sub>2</sub> )		
Certified Gas (%)	Instrument Reading (%)	Uncertainty (%)
5.1	5.0	0.43
15.0	14.9	0.70
50.0	50.0	1.1

Oxygen (O <sub>2</sub> )		
Certified Gas (%)	Instrument Reading (%)	Uncertainty (%)
20.9	20.9	0.31

The inwards assessment was carried out 14-Jun-2017.

The maximum adjustment is larger than the inwards assessment uncertainty.

Inwards assessment data is available if requested.

All concentrations are molar.

CH<sub>4</sub>, CO<sub>2</sub> readings recorded at : 37.2 °C ± 1.5 °C

O<sub>2</sub> reading recorded at : 26.8 °C ± 1.5 °C

Barometric Pressure : 1012 mbar ± 3 mbar

Method of Test : The analyser is calibrated in a temperature controlled chamber using a series of reference gases, in compliance with procedure LP004.

This certificate is issued in accordance with the laboratory accreditation requirements of the United Kingdom Accreditation Service. It provides traceability of measurement to the SI system of units and/or to units of measurement realised at the National Physical Laboratory or other recognised national metrology institutes. This certificate may not be reproduced other than in full, except with the prior written approval of the Issuing laboratory.

Page 1 of 2 | LP015GIUKAS-2.2

# CERTIFICATION OF CALIBRATION

Date Of Calibration: 20-Jun-2017 Certificate Number: G503226\_2/18640



# Geotech

ISSUED BY: GEOTECHNICAL INSTRUMENTS (UK) LTD

The reported expanded uncertainty is based on a standard uncertainty multiplied by a coverage factor of  $k=2$ , providing a level of confidence of approximately 95%. The uncertainty evaluation has been carried out in accordance with UKAS requirements.

Calibrations marked 'Non-UKAS Accredited results' on this certificate have been included for completeness.

### Non-UKAS Accredited results:

Barometer (mbar)	
Reference	Instrument Reading
1012	1014

Approved by Signatory

Dawn Hemings


Laboratory Inspection

This certificate is issued in accordance with the laboratory accreditation requirements of the United Kingdom Accreditation Service. It provides traceability of measurement to the SI system of units and/or to units of measurement realised at the National Physical Laboratory or other recognised national metrology institutes. This certificate may not be reproduced other than in full, except with the prior written approval of the issuing laboratory.



## **Appendix I**

### **Landfill Gas Monitoring Results and Graphical Plots**

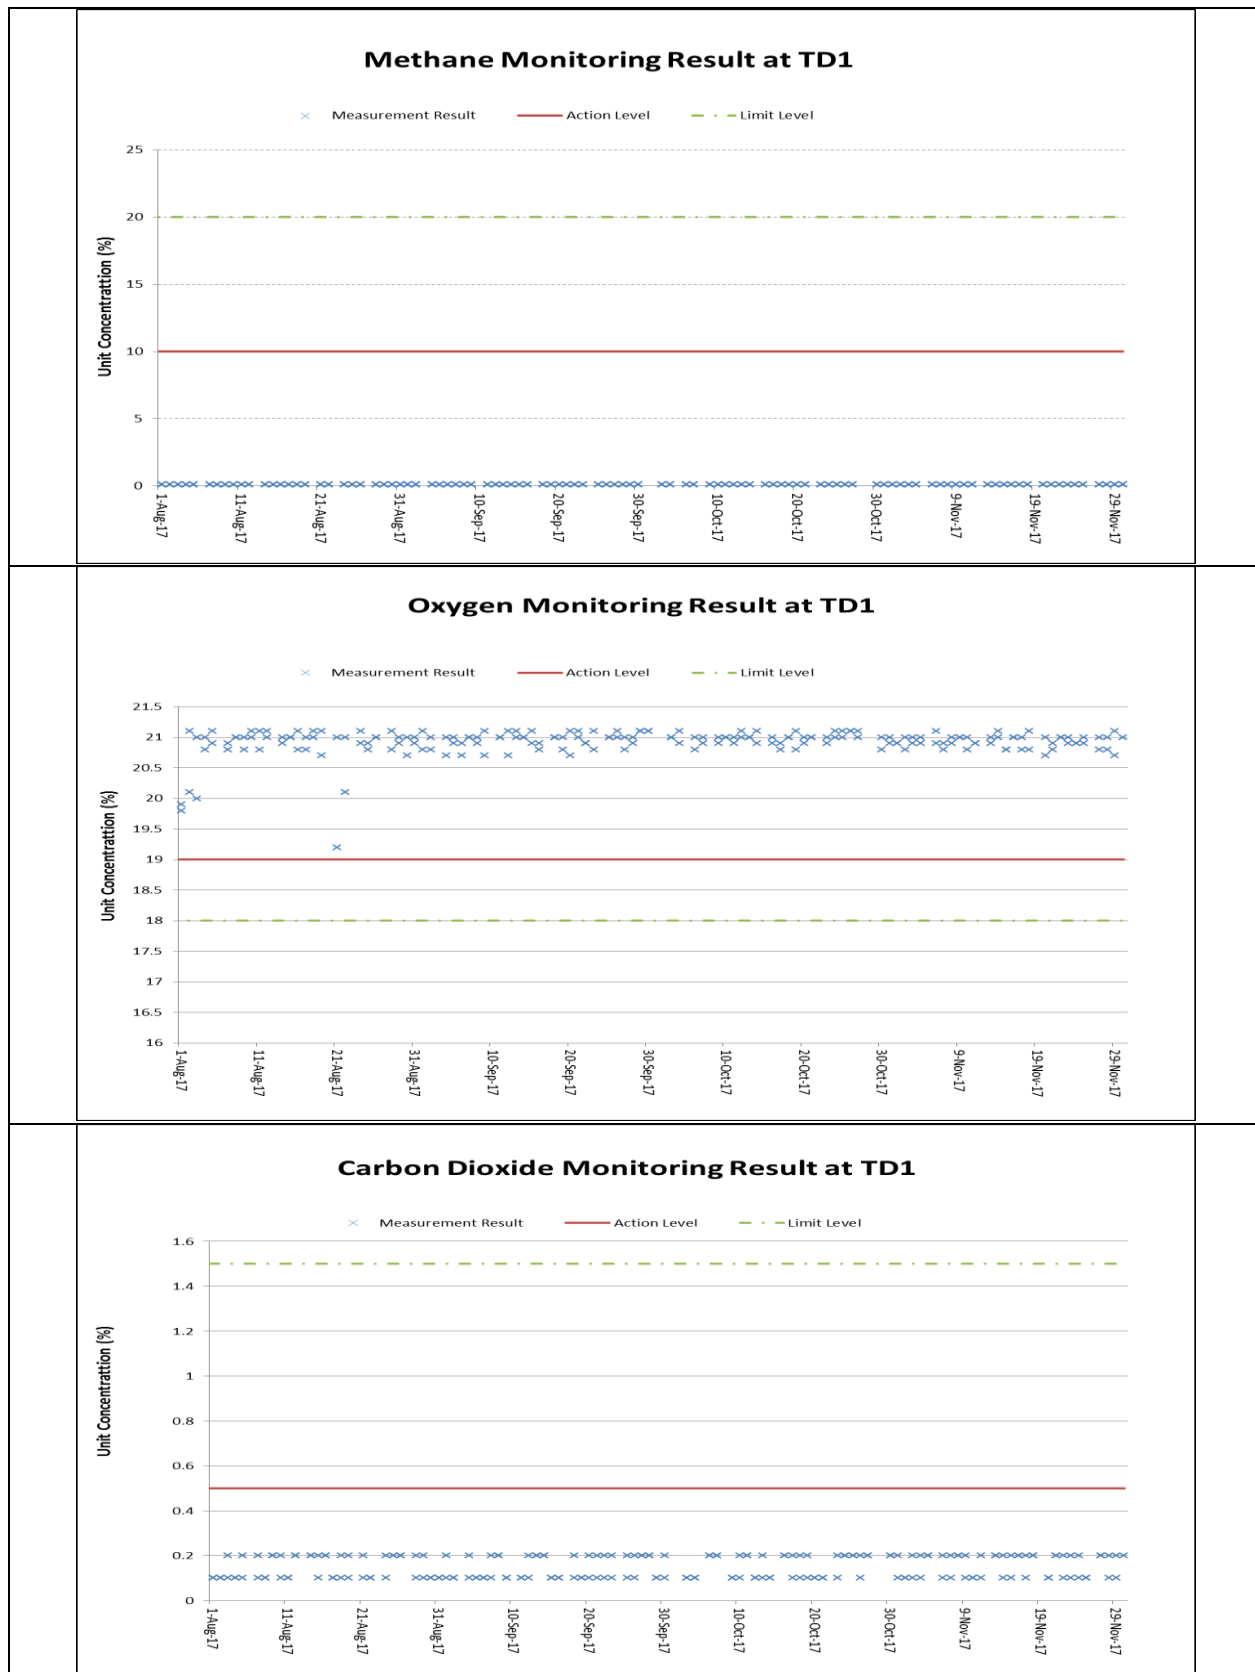

**Annotation:**  
 During 1 to 30 November 2017, major construction activity at TD1 and the specified works included excavation, stitching, blinding, formworking, steel-fixing and concreting. The weather condition varied from sunny to rainy. The monitoring data was provided by the Contractor followed to their QA/QC control.

**Landfill Gas Monitoring Results (TD1)**

Monitoring Location	Date	Time	Weather	Temperature (°C)	Methane (%)			Oxygen (%)			Carbon Dioxide (%)		
					Measurement Result	Action Level	Limit Level	Measurement Result	Action Level	Limit Level	Measurement Result	Action Level	Limit Level
TD1	1/11/2017	8:00		20	0.1	10	20	21	19	18	0.2	0.5	1.5
	1/11/2017	14:00	Sunny	27	0.1	10	20	20.9	19	18	0.1	0.5	1.5
	2/11/2017	8:00		21	0.1	10	20	20.9	19	18	0.1	0.5	1.5
	2/11/2017	14:00	Sunny	28	0.1	10	20	20.8	19	18	0.1	0.5	1.5
	3/11/2017	8:00		22	0.1	10	20	21	19	18	0.2	0.5	1.5
	3/11/2017	14:00	Sunny	28	0.1	10	20	20.9	19	18	0.2	0.5	1.5
	4/11/2017	8:00		21	0.1	10	20	21	19	18	0.1	0.5	1.5
	4/11/2017	14:00	Sunny	26	0.1	10	20	20.9	19	18	0.2	0.5	1.5
	6/11/2017	8:00		21	0.1	10	20	21	19	18	0.2	0.5	1.5
	6/11/2017	14:00	Cloudy	26	0.1	10	20	20.9	19	18	0.1	0.5	1.5
	7/11/2017	8:00		22	0.1	10	20	21.1	19	18	0.2	0.5	1.5
	7/11/2017	14:00	Fine	26	0.1	10	20	20.8	19	18	0.2	0.5	1.5
	8/11/2017	8:00		23	0.1	10	20	20.9	19	18	0.1	0.5	1.5
	8/11/2017	14:00	Fine	27	0.1	10	20	21	19	18	0.2	0.5	1.5
	9/11/2017	8:00		23	0.1	10	20	20.9	19	18	0.2	0.5	1.5
	9/11/2017	14:00	Cloudy	27	0.1	10	20	21	19	18	0.1	0.5	1.5
	10/11/2017	8:00		23	0.1	10	20	21	19	18	0.2	0.5	1.5
	10/11/2017	14:00	Sunny	28	0.1	10	20	20.8	19	18	0.1	0.5	1.5
	11/11/2017	8:00		23	0.1	10	20	21	19	18	0.1	0.5	1.5
	11/11/2017	14:00	Sunny	28	0.1	10	20	20.9	19	18	0.1	0.5	1.5
	13/11/2017	8:00		21	0.1	10	20	20.9	19	18	0.2	0.5	1.5
	13/11/2017	14:00	Cloudy	24	0.1	10	20	21	19	18	0.2	0.5	1.5
	14/11/2017	8:00		22	0.1	10	20	20.9	19	18	0.2	0.5	1.5
	14/11/2017	14:00	Sunny	24	0.1	10	20	21	19	18	0.2	0.5	1.5
	15/11/2017	8:00		22	0.1	10	20	21.1	19	18	0.1	0.5	1.5
	15/11/2017	14:00	Fine	24	0.1	10	20	20.8	19	18	0.2	0.5	1.5
	16/11/2017	8:00		22	0.1	10	20	20.8	19	18	0.1	0.5	1.5
	16/11/2017	14:00	Sunny	27	0.1	10	20	21	19	18	0.2	0.5	1.5
	17/11/2017	8:00		22	0.1	10	20	21	19	18	0.2	0.5	1.5
	17/11/2017	14:00	Sunny	26	0.1	10	20	20.8	19	18	0.2	0.5	1.5
18/11/2017	8:00		20	0.1	10	20	21	19	18	0.1	0.5	1.5	
18/11/2017	14:00	Cloudy	27	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
20/11/2017	8:00		18	0.1	10	20	20.8	19	18	0.2	0.5	1.5	
20/11/2017	14:00	Sunny	20	0.1	10	20	20.7	19	18	0.1	0.5	1.5	
21/11/2017	8:00		17	0.1	10	20	21	19	18	0.1	0.5	1.5	
21/11/2017	14:00	Sunny	21	0.1	10	20	20.8	19	18	0.2	0.5	1.5	
22/11/2017	8:00		17	0.1	10	20	20.9	19	18	0.2	0.5	1.5	
22/11/2017	14:00	Sunny	23	0.1	10	20	21	19	18	0.1	0.5	1.5	
23/11/2017	8:00		16	0.1	10	20	21	19	18	0.2	0.5	1.5	
23/11/2017	14:00	Sunny	20	0.1	10	20	20.9	19	18	0.2	0.5	1.5	
24/11/2017	8:00		16	0.1	10	20	21	19	18	0.1	0.5	1.5	
24/11/2017	14:00	Sunny	21	0.1	10	20	20.9	19	18	0.2	0.5	1.5	
25/11/2017	8:00		17	0.1	10	20	20.9	19	18	0.1	0.5	1.5	
25/11/2017	14:00	Sunny	19	0.1	10	20	21	19	18	0.1	0.5	1.5	
27/11/2017	8:00		18	0.1	10	20	20.9	19	18	0.1	0.5	1.5	
27/11/2017	14:00	Hazy	22	0.1	10	20	20.8	19	18	0.2	0.5	1.5	
28/11/2017	8:00		21	0.1	10	20	21	19	18	0.2	0.5	1.5	
28/11/2017	14:00	Sunny	25	0.1	10	20	20.8	19	18	0.2	0.5	1.5	
29/11/2017	8:00		21	0.1	10	20	21	19	18	0.1	0.5	1.5	
29/11/2017	14:00	Sunny	26	0.1	10	20	20.7	19	18	0.1	0.5	1.5	
30/11/2017	8:00		21	0.1	10	20	21.1	19	18	0.2	0.5	1.5	
30/11/2017	14:00	Sunny	25	0.1	10	20	21	19	18	0.2	0.5	1.5	

Remark:

Parameter	Criteria	Measurement
Oxygen	Action Level	< 19%
	Limit Level	< 18%
Methane	Action Level	> 10% LEL (> 0.5% v/v)
	Limit Level	> 20% LEL (> 1% v/v)
Carbon Dioxide	Action Level	> 0.5%
	Limit Level	> 1.5%

## **Appendix J**

### **Investigation Report for Exceedance**

**Contract No. HY/2013/12**  
**Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works**

**Investigation Report on Action or Limit Level Non-compliance**

<b>Date</b>	21 October 2017		
<b>Environmental Aspect</b>	Air Quality		
<b>Parameter</b>	1-hour TSP	24-hour TSP	
<b>Monitoring Location</b>	ASR1 (Tuen Mun Fireboat Station)		
<b>Measurement Period</b>	10:47 – 11:47	11:49 – 12:49	13:53 – 13:53
<b>Action Level (ug/m<sup>3</sup>)</b>	331	331	213
<b>Limit Level (ug/m<sup>3</sup>)</b>	500	500	260
<b>Measured Level (ug/m<sup>3</sup>)</b>	<b>372</b>	<b>439</b>	<b>220</b>
<b>Exceedance</b>	<b>Action Level</b>	<b>Action Level</b>	<b>Action Level</b>
<b>Possible reason for Action or Limit Level Non-compliance</b>	<ol style="list-style-type: none"> <li>1. According to site information provided by CRBC-Kaden JV, road and drainage works at Platform 19 &amp; Retaining Wall B, removal of weeds at Lung Mun Road near Butterfly Beach Laundry, housekeeping works at Retaining Wall B &amp; Slope 170 and construction of column at Portion F were conducted on 21 October 2017.</li> <li>2. To reduce dust impact arising from the construction, mitigation measures for construction dust control were implemented. They include the followings:- <ul style="list-style-type: none"> <li>• water trucks were arranged on haul road to keep road surface wet (refer to photo 1, 7 and water spraying record)</li> <li>• for un-accessible area, water spraying by workers was provided (refer to photo 2 and water spraying record)</li> <li>• Hydro seeding or covered part of the exposed slopes and stockpile by tarpaulin sheet (refer to Photo 3 to 5)</li> <li>• to set speed control at 8 km/hr for all vehicles using the haul road (refer to photo 6)</li> </ul> </li> <li>3. During site inspection on 24 October 2017, it was observed that the dust mitigation measures were implemented and the site condition is acceptable. Photo showing the implemented dust mitigation measures on 24 October 2017 is shown in photo record.</li> <li>4. Reviewing the monitoring data on 21 October 2017, only exceedances were recorded in the monitoring station ASR1 which is most apart from the construction area of Contract No. HY/2013/12 and no exceedance were recorded at the nearby monitoring stations. The highest 1-Hr TSP concentration level was recorded between 11:49 to 12:49 which is the lunch period (12:00-13:00) of the construction site most of the construction activities were stopped. Similar construction activities were undertaken on 18 and 24 October 2017 and no exceedance were record in both 1-Hr and 24-Hr TSP monitoring. (Ref. to Location Plan)</li> <li>5. Also the contractor was properly implemented the dust mitigation measure under EMIS requirement. Therefore we considered that the cause of exceedance is due to other pollutant source rather than the construction site.</li> </ol>		

	6. Based on above investigation, the exceedance is unlikely related to the Contract work and no corrective action was required accordingly.
<b>Action to be taken</b>	ET will continue regular audit and inspection for the implemented dust mitigation measures during the construction period.


**Prepared By :** T.W. Tam

**Designation :** Environmental Team Leader


**Signature :** 

**Date :** 8 November 2017

**Photo Record**

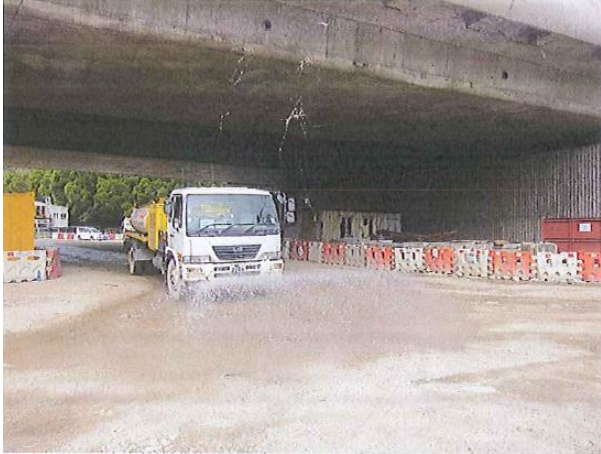

**Photo 1** Watering of haul road by water truck to keep road surface wet

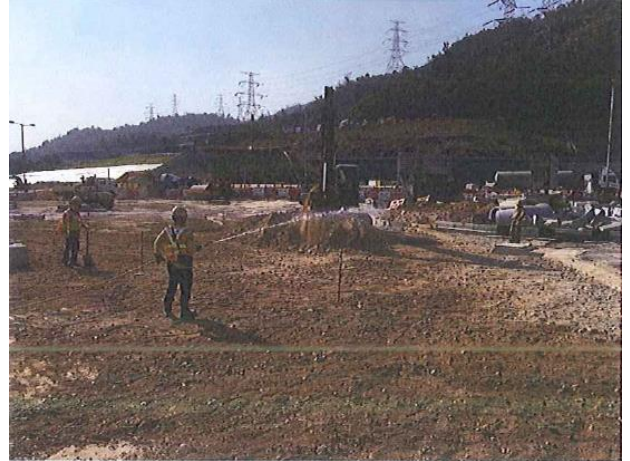

**Photo 2** Water spraying by worker for un-accessible area.



**Photo 3** Covered part of the exposed slopes and stockpile by tarpaulin sheet.



**Photo 4** Hydro seeding for the exposed slope at slope 170.



**Photo 5** Covered part of the exposed slopes and stockpile by tarpaulin sheet.



**Photo 6** Set speed control at ~8km/hr for all vehicles using the haul road



**Photo 7** Watering of haul road by water truck to keep road surface wet was observed during the site inspection on 24 October 2017



**Photo 8** Housekeeping works at Retaining Wall B.



**Photo 9** Removal of weeds at Lung Mun Road near Butterfly Beach Laundry.



**Photo 10** Road works at Retaining Wall B.



**Photo 11** Drainage works at Platform 19.



**Photo 12** Road works at Retaining Wall B.





**Photo 13** Construction of column at Portion F.



**Photo 14** Construction of column at Portion F.

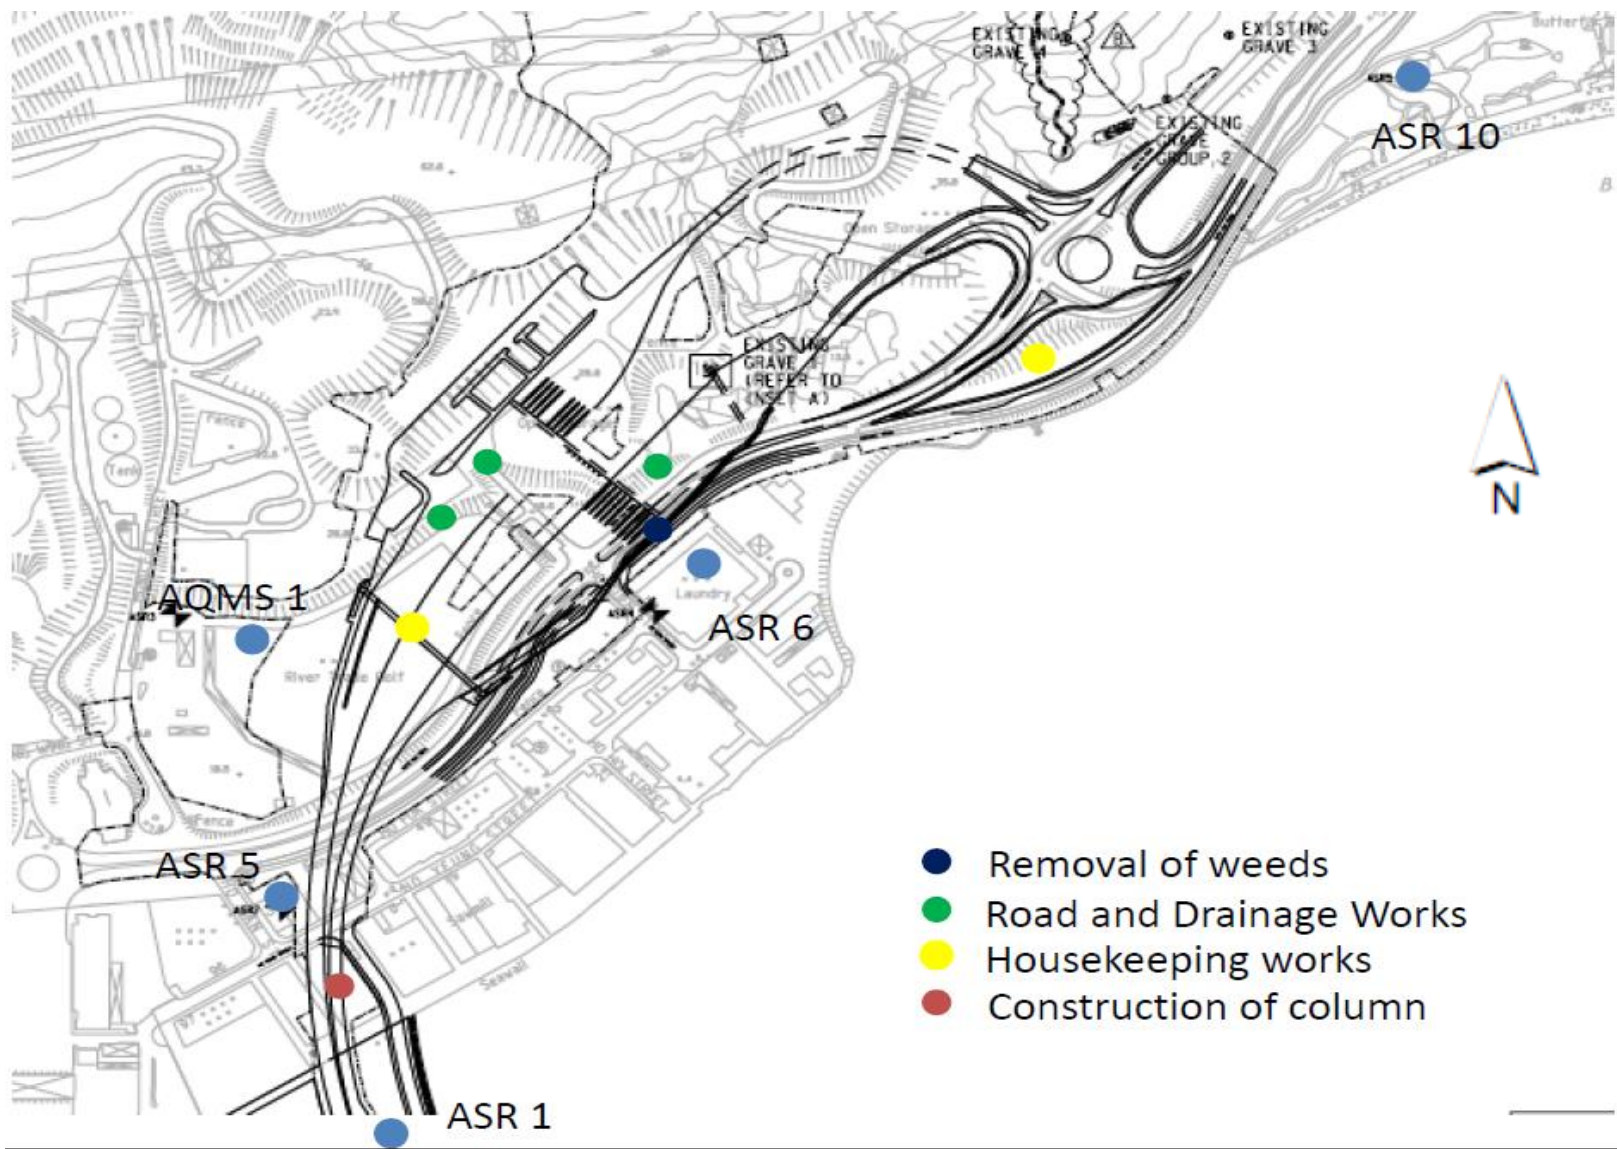


Figure 1. Location Plan

**Table 1. 1-Hr and 24-Hr TSP Monitoring Result of 21 October 2017**

TMCLKL	HY/2012/08	21/10/2017	AQMS1	Sunny	10:58	1-hour TSP	61	ug/m3
TMCLKL	HY/2012/08	21/10/2017	AQMS1	Sunny	12:00	1-hour TSP	41	ug/m3
TMCLKL	HY/2012/08	21/10/2017	AQMS1	Sunny	13:02	1-hour TSP	110	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR1	Sunny	10:47	1-hour TSP	372	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR1	Sunny	11:49	1-hour TSP	439	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR1	Sunny	12:51	1-hour TSP	307	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR10	Sunny	10:12	1-hour TSP	307	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR10	Sunny	11:14	1-hour TSP	72	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR10	Sunny	12:16	1-hour TSP	219	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR5	Sunny	10:35	1-hour TSP	181	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR5	Sunny	11:37	1-hour TSP	168	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR5	Sunny	12:39	1-hour TSP	133	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR6	Sunny	10:24	1-hour TSP	150	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR6	Sunny	11:26	1-hour TSP	88	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR6	Sunny	12:28	1-hour TSP	156	ug/m3
TMCLKL	HY/2012/08	21/10/2017	AQMS1	Sunny	14:04	24-hour TSP	70	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR1	Sunny	13:53	24-hour TSP	220	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR10	Sunny	13:18	24-hour TSP	72	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR5	Sunny	13:41	24-hour TSP	103	ug/m3
TMCLKL	HY/2012/08	21/10/2017	ASR6	Sunny	13:30	24-hour TSP	101	ug/m3

# 地盆人手灑水記錄表(2017)

地點:	星期日	星期一	星期二	星期三	星期四	星期五	星期六
Slope Area	10月15日	10月16日	10月17日	10月18日	10月19日	10月20日	10月21日
8:00 - 8:30		✓	✓	✓	✓	✓	✓
8:30 - 9:00		✓	✓	✓	✓	✓	✓
9:00 - 9:30		✓	✓	✓	✓	✓	✓
9:30 - 10:00		✓	✓	✓	✓	✓	✓
10:00 - 10:30		✓	✓	✓	✓	✓	✓
10:30 - 11:00		✓	✓	✓	✓	✓	✓
11:00 - 11:30		✓	✓	✓	✓	✓	✓
11:30 - 12:00		✓	✓	✓	✓	✓	✓
12:00 - 12:30		✓	✓	✓	✓	✓	✓
12:30 - 13:00		✓	✓	✓	✓	✓	✓
13:00 - 13:30		✓	✓	✓	✓	✓	✓
13:30 - 14:00		✓	✓	✓	✓	✓	✓
14:00 - 14:30		✓	✓	✓	✓	✓	✓
14:30 - 15:00		✓	✓	✓	✓	✓	✓
15:00 - 15:30		✓	✓	✓	✓	✓	✓
15:30 - 16:00		✓	✓	✓	✓	✓	✓
16:00 - 16:30		✓	✓	✓	✓	✓	✓
16:30 - 17:00		✓	✓	✓	✓	✓	✓
17:00 - 17:30		✓	✓	✓	✓	✓	✓
17:30 - 18:00		✓	✓	✓	✓	✓	✓

Verified by Tommy Law (IES)

Date

*TL*

23/10/2017

# 地盆人手灑水記錄表(2017)

地點: <i>Cartry Rubbex</i>	星期日	星期一	星期二	星期三	星期四	星期五	星期六
	10月15日	10月16日	10月17日	10月18日	10月19日	10月20日	10月21日
8:00 - 8:30		✓	✓	✓	✓	✓	✓
8:30 - 9:00		✓	✓	✓	✓	✓	✓
9:00 - 9:30		✓	✓	✓	✓	✓	✓
9:30 - 10:00		✓	✓	✓	✓	✓	✓
10:00 - 10:30		✓	✓	✓	✓	✓	✓
10:30 - 11:00		✓	✓	✓	✓	✓	✓
11:00 - 11:30		✓	✓	✓	✓	✓	✓
11:30 - 12:00		✓	✓	✓	✓	✓	✓
12:00 - 12:30		✓	✓	✓	✓	✓	✓
12:30 - 13:00		✓	✓	✓	✓	✓	✓
13:00 - 13:30		✓	✓	✓	✓	✓	✓
13:30 - 14:00		✓	✓	✓	✓	✓	✓
14:00 - 14:30		✓	✓	✓	✓	✓	✓
14:30 - 15:00		✓	✓	✓	✓	✓	✓
15:00 - 15:30		✓	✓	✓	✓	✓	✓
15:30 - 16:00		✓	✓	✓	✓	✓	✓
16:00 - 16:30		✓	✓	✓	✓	✓	✓
16:30 - 17:00		✓	✓	✓	✓	✓	✓
17:00 - 17:30		✓	✓	✓	✓	✓	✓
17:30 - 18:00		✓	✓	✓	✓	✓	✓

*陳偉斌 Rex Chan Rex Chan Rex Chan Rex Chan Rex Chan Rex Chan Rex Chan Rex Chan*

Verified by *Tommy Law (ES)*  
 Date *23/10/17*

KL 7286

# 地盆水車灑水記錄表(2017)

	星期日	星期一	星期二	星期三	星期四	星期五	星期六
	10月15日	10月16日	10月17日	10月18日	10月19日	10月20日	10月21日
8:00 - 8:30		✓	✓	✓	✓	✓	✓
8:30 - 9:00		✓	✓	✓	✓	✓	✓
9:00 - 9:30		✓	✓	✓	✓	✓	✓
9:30 - 10:00		✓	✓	✓	✓	✓	✓
10:00 - 10:30		✓	✓	✓	✓	✓	✓
10:30 - 11:00		✓	✓	✓	✓	✓	✓
11:00 - 11:30		✓	✓	✓	✓	✓	✓
11:30 - 12:00		✓	✓	✓	✓	✓	✓
12:00 - 12:30		✓	✓	✓	✓	✓	✓
12:30 - 13:00		✓	✓	✓	✓	✓	✓
13:00 - 13:30		✓	✓	✓	✓	✓	✓
13:30 - 14:00		✓	✓	✓	✓	✓	✓
14:00 - 14:30		✓	✓	✓	✓	✓	✓
14:30 - 15:00		✓	✓	✓	✓	✓	✓
15:00 - 15:30		✓	✓	✓	✓	✓	✓
15:30 - 16:00		✓	✓	✓	✓	✓	✓
16:00 - 16:30		✓	✓	✓	✓	✓	✓
16:30 - 17:00		✓	✓	✓	✓	✓	✓
17:00 - 17:30		✓	✓	✓	✓	✓	✓
17:30 - 18:00		✓	✓	✓	✓	✓	✓

Lai Kam Yui   Lai Kam Yui   Lai Kam Yui   Lai Kam Yui   Lai Kam Yui   Lai Kam Yui   Lai Kam Yui

Verified by Tommy Lew (ES) /   
 Date 23/10/2017

62837

# 地盆水車灑水記錄表(2017)

星期日	星期一	星期二	星期三	星期四	星期五	星期六
10月15日	10月16日	10月17日	10月18日	10月19日	10月20日	10月21日
8:00 - 8:30	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓

張 家 張 張 張 張 張

Verified by Tommy Law (ES)

Date

*[Signature]*

23/10/17





**Contract No. HY/2013/12**  
**Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works**

**Investigation Report on Action or Limit Level Non-compliance**

<b>Date</b>	27 October 2017	
<b>Environmental Aspect</b>	Air Quality	
<b>Parameter</b>	1-hour TSP	
<b>Monitoring Location</b>	ASR5 (Pillar Point Fire Station)	ASR6 (Butterfly Beach Laundry)
<b>Measurement Period</b>	15:42-16:42	15:32-16:32
<b>Action Level (ug/m<sup>3</sup>)</b>	340	340
<b>Limit Level (ug/m<sup>3</sup>)</b>	500	500
<b>Measured Level (ug/m<sup>3</sup>)</b>	<b>368</b>	<b>388</b>
<b>Exceedance</b>	<b>Action Level</b>	<b>Action Level</b>
<b>Possible reason for Action or Limit Level Non-compliance</b>	<ol style="list-style-type: none"> <li>1. According to site information provided by CRBC-Kaden JV, road and drainage works at Platform 19, construction of bus shelter at Retaining Wall B, housekeeping works under Retaining Wall B, road pavement works at Lung Mun Road and construction of column at Portion F were conducted on 27 October 2017.</li> <li>2. To reduce dust impact arising from the construction, mitigation measures for construction dust control were implemented. They include the followings:- <ul style="list-style-type: none"> <li>• water trucks were arranged on haul road to keep road surface wet (refer to photo 1, 9, 12, 13 and water spraying record)</li> <li>• for un-accessible area, water spraying by workers was provided (refer to photo 2, 10 and water spraying record)</li> <li>• Hydro seeding or covered part of the exposed slopes and stockpile by tarpaulin sheet (refer to Photo 3, 7, 8 and 11)</li> <li>• to set speed control at 8 km/hr for all vehicles using the haul road (refer to photo 6)</li> </ul> </li> <li>3. During site inspection on 24 &amp; 31 October 2017, it was observed that the dust mitigation measures were implemented and the site condition is acceptable. Photo showing the implemented dust mitigation measures on 24 &amp; 31 October 2017 is shown in photo record.</li> <li>4. According to the weather station setting up at ASR5 under Contract No. HY/2012/08, north-westerly to north-easterly wind at 1.3 to 2.2 m/s was blowing between 13:00 to 15:00. All the monitoring stations were located at the downstream of the construction area but no exceedance was record. While the exceedances were recorded in ASR5 and ASR6 at around the monitoring period from 15:30 to 16:30, the wind direction was changed from north-easterly to south-easterly. Most of the construction areas were located at the downstream of the monitoring station ASR5 &amp; ASR6 except Portion F.</li> <li>5. The works area Portion F was located at the upstream of the monitoring station ASR5 during the exceedance was recorded</li> </ol>	

	<p>but only construction of column which include mobilize materials and installing metal formworks was undertaken in that area and most site area at Portion F was hard paved which is unlikely to create heavy construction dust impact. (Ref. to Location Plan and Photo 9 &amp; 10)</p> <p>6. Also the contractor was properly implemented the dust mitigation measure under EMIS requirement. Therefore we considered that the cause of exceedance is due to other pollutant source rather than the construction site.</p> <p>7. Based on above investigation, the exceedance is unlikely related to the Contract work and no corrective action was required accordingly.</p>
<b>Action to be taken</b>	ET will continue regular audit and inspection for the implemented dust mitigation measures during the construction period.

**Prepared By :** T.W. Tam

**Designation :** Environmental Team Leader

**Signature :**  \_\_\_\_\_

**Date :** 10 November 2017

## Photo Record



**Photo 1** Watering of haul road by water truck to keep road surface wet



**Photo 2** Water spraying by worker for un-accessible area.



**Photo 3** Covered part of the exposed slopes and stockpile by tarpaulin sheet.



**Photo 4** Hydro seeding for the exposed slope at slop 170



**Photo 5** Covered part of the exposed slopes and stockpile by tarpaulin sheet.



**Photo 6** Set speed control at ~8km/hr for all vehicles using the haul road



**Photo 7** Photo taken of hydro seeding for the exposed sloop at slop 170 during the site inspection on 24 October 2017



**Photo 8** Covered part of the exposed slopes and stockpile by tarpaulin sheet was observed in the site inspection on 24 October 2017



**Photo 9** Watering of haul road by water truck to keep road surface wet was observed during the site inspection on 24 October 2017



**Photo 10** Watering of haul road to keep road surface wet was observed at Portion F during the site inspection on 31 October 2017



**Photo 11** Photo taken of hydro seeding for the exposed sloop at slop 170 during the site inspection on 31 October 2017



**Photo 12** Watering of haul road by water truck to keep road surface wet was observed during the site inspection on 31 October 2017



**Photo 13** Two water truck were in operation during the site inspection on 31 October 2017



**Photo 14** No dust emitted for the Portion F was observed during the site inspection on 31 October 2017 and the works area was clean and tidy



**Photo 15** Construction of bus shelter at Retaining Wall B.



**Photo 16** Road pavements works at Lung Mun Road.



**Photo 17** Drainage works at Platform 19.



**Photo 18** Construction of column at Portion F



**Photo 19** Housekeeping works at existing Grave G1 under Retaining Wall B.



**Photo 20** Housekeeping works at existing Grave G1 under Retaining Wall B.



**Photo 21** Construction of column at Portion F and most works area was hard paved.



**Photo 22** Construction of column at Portion F and most works area was hard paved.

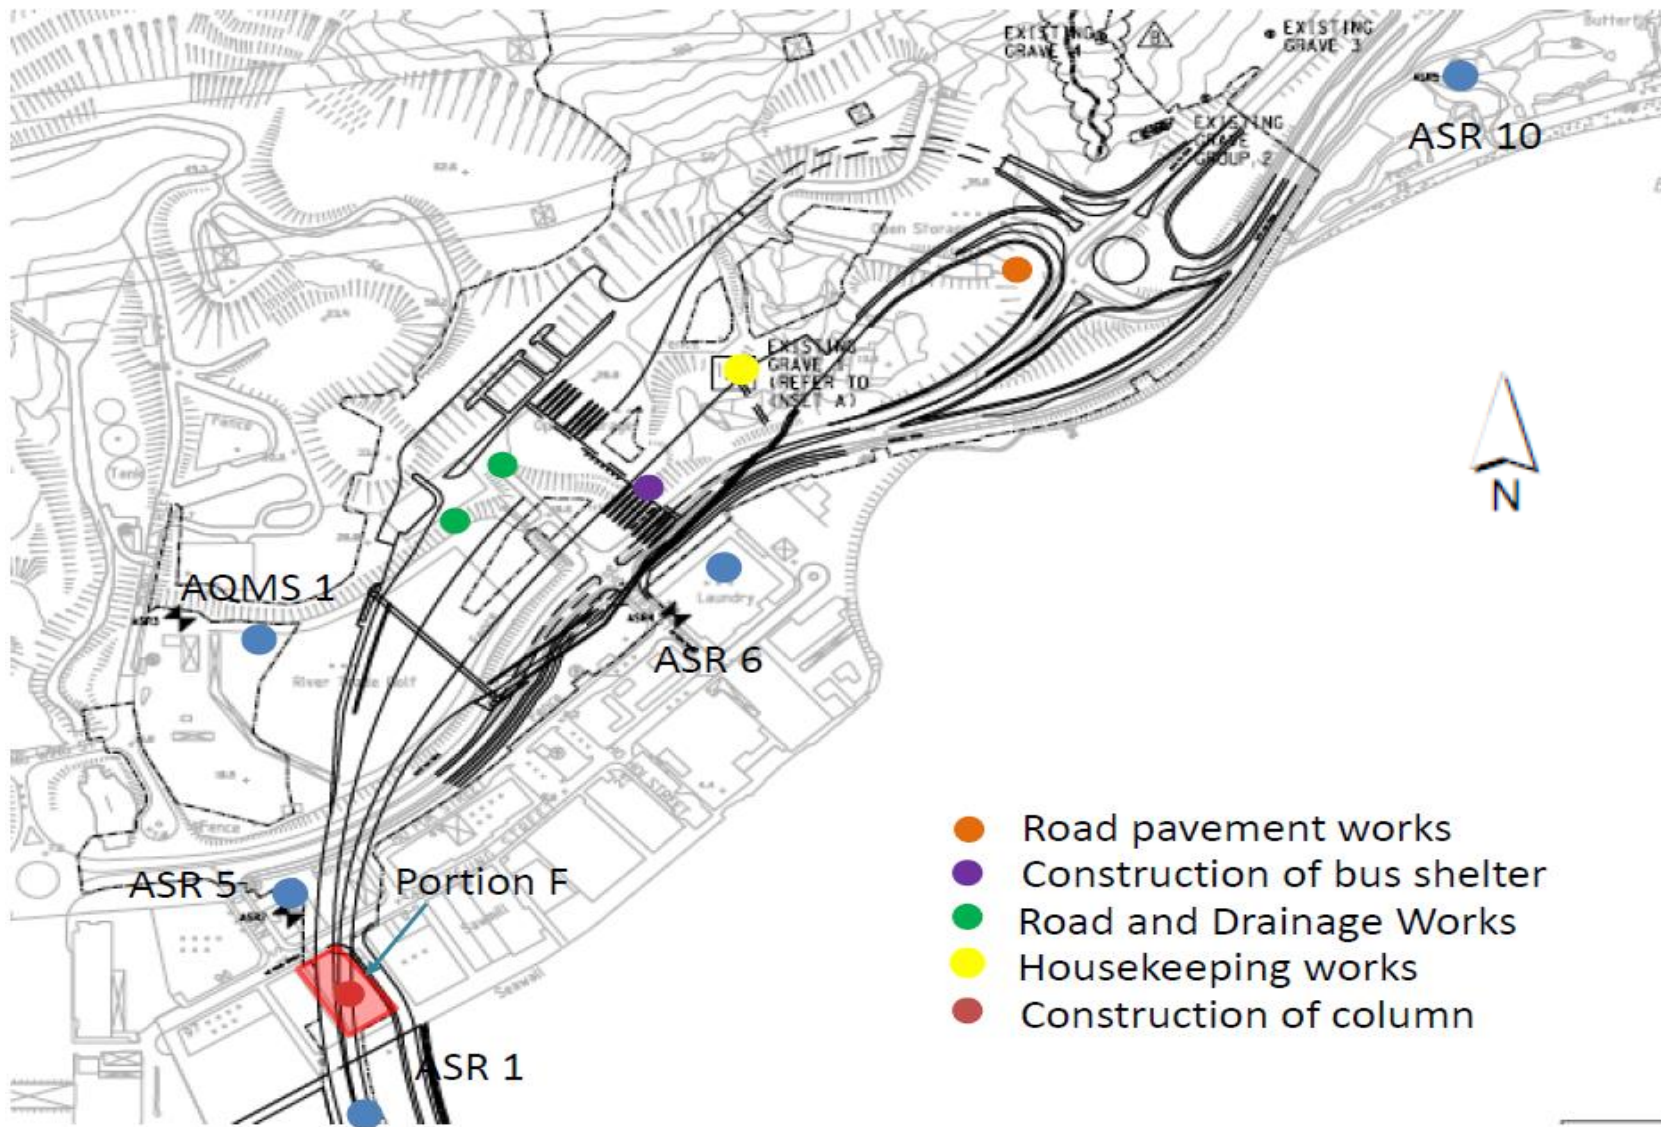


Figure 1. Location Plan

**Table 1. 1-Hr TSP Monitoring Result of 27 October 2017**

TMCLKL	HY/2012/08	27/10/2017	AQMS1	Sunny	14:02	1-hour TSP	109	ug/m3
TMCLKL	HY/2012/08	27/10/2017	AQMS1	Sunny	15:04	1-hour TSP	227	ug/m3
TMCLKL	HY/2012/08	27/10/2017	AQMS1	Sunny	16:06	1-hour TSP	234	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR1	Sunny	13:51	1-hour TSP	228	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR1	Sunny	14:53	1-hour TSP	225	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR1	Sunny	15:55	1-hour TSP	293	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR10	Sunny	13:17	1-hour TSP	123	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR10	Sunny	14:14	1-hour TSP	123	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR10	Sunny	15:21	1-hour TSP	148	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR5	Sunny	13:39	1-hour TSP	207	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR5	Sunny	14:41	1-hour TSP	219	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR5	Sunny	15:42	1-hour TSP	368	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR6	Sunny	13:28	1-hour TSP	152	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR6	Sunny	14:30	1-hour TSP	154	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR6	Sunny	15:32	1-hour TSP	388	ug/m3
TMCLKL	HY/2012/08	27/10/2017	AQMS1	Sunny	17:08	24-hour TSP	94	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR1	Sunny	16:57	24-hour TSP	191	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR10	Sunny	16:23	24-hour TSP	91	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR5	Sunny	16:44	24-hour TSP	119	ug/m3
TMCLKL	HY/2012/08	27/10/2017	ASR6	Sunny	16:34	24-hour TSP	108	ug/m3

**Table 2. Wind Direction and Speed data during 1-Hr TSP Monitoring**

Date	Time	Average of Wind Speed (m/s)	Average of Wind Direction (degree)
27/10/2017	13:00	1.8	40
27/10/2017	14:00	2.2	255
27/10/2017	15:00	1.3	19
27/10/2017	16:00	1.8	119

**Remarks:**

Wind speed and direction data was extracted from the weather station located at ASR5 set up by ET of Contract HY/2012/08



# 地盆人手灑水記錄表(2017)

地點:	星期日	星期一	星期二	星期三	星期四	星期五	星期六
10月22日	10月23日	10月24日	10月25日	10月26日	10月27日	10月28日	
8:00 - 8:30	✓	✓	✓	✓	✓	✓	
8:30 - 9:00	✓	✓	✓	✓	✓	✓	
9:00 - 9:30	✓	✓	✓	✓	✓	✓	
9:30 - 10:00	✓	✓	✓	✓	✓	✓	
10:00 - 10:30	✓	✓	✓	✓	✓	✓	
10:30 - 11:00	✓	✓	✓	✓	✓	✓	
11:00 - 11:30	✓	✓	✓	✓	✓	✓	
11:30 - 12:00	✓	✓	✓	✓	✓	✓	
12:00 - 12:30	✓	✓	✓	✓	✓	✓	
12:30 - 13:00	✓	✓	✓	✓	✓	✓	
13:00 - 13:30	✓	✓	✓	✓	✓	✓	
13:30 - 14:00	✓	✓	✓	✓	✓	✓	
14:00 - 14:30	✓	✓	✓	✓	✓	✓	
14:30 - 15:00	✓	✓	✓	✓	✓	✓	
15:00 - 15:30	✓	✓	✓	✓	✓	✓	
15:30 - 16:00	✓	✓	✓	✓	✓	✓	
16:00 - 16:30	✓	✓	✓	✓	✓	✓	
16:30 - 17:00	✓	✓	✓	✓	✓	✓	
17:00 - 17:30	✓	✓	✓	✓	✓	✓	
17:30 - 18:00	✓	✓	✓	✓	✓	✓	

陳偉斌 陳偉斌 陳偉斌 陳偉斌 陳偉斌 陳偉斌 陳偉斌

Rex Chan Rex Chan Rex Chan Rex Chan Rex Chan Rex Chan Rex Chan

# 地盆人手灑水記錄表(2017)

星期日	星期一	星期二	星期三	星期四	星期五	星期六
10月22日	10月23日	10月24日	10月25日	10月26日	10月27日	10月28日
地點: <i>Slope Area</i>						
8:00 - 8:30	✓	✓	✓	✓	✓	
8:30 - 9:00	✓	✓	✓	✓	✓	
9:00 - 9:30	✓	✓	✓	✓	✓	
9:30 - 10:00	✓	✓	✓	✓	✓	
10:00 - 10:30	✓	✓	✓	✓	✓	
10:30 - 11:00	✓	✓	✓	✓	✓	
11:00 - 11:30	✓	✓	✓	✓	✓	
11:30 - 12:00	✓	✓	✓	✓	✓	
12:00 - 12:30	✓	✓	✓	✓	✓	
12:30 - 13:00	✓	✓	✓	✓	✓	
13:00 - 13:30	✓	✓	✓	✓	✓	
13:30 - 14:00	✓	✓	✓	✓	✓	
14:00 - 14:30	✓	✓	✓	✓	✓	
14:30 - 15:00	✓	✓	✓	✓	✓	
15:00 - 15:30	✓	✓	✓	✓	✓	
15:30 - 16:00	✓	✓	✓	✓	✓	
16:00 - 16:30	✓	✓	✓	✓	✓	
16:30 - 17:00	✓	✓	✓	✓	✓	
17:00 - 17:30	✓	✓	✓	✓	✓	
17:30 - 18:00	✓	✓	✓	✓	✓	

*Tommy Lau*

*TL*

Verified by Tommy Lau (ES)

20/10/2017

Date

# 地盆人手灑水記錄表(2017)

地點:	星期日	星期一	星期二	星期三	星期四	星期五	星期六
Porter M.	10月22日	10月23日	10月24日	10月25日	10月26日	10月27日	10月28日
8:00 - 8:30		✓	✓	✓	✓	✓	
8:30 - 9:00		✓	✓	✓	✓	✓	
9:00 - 9:30		✓	✓	✓	✓	✓	
9:30 - 10:00		✓	✓	✓	✓	✓	
10:00 - 10:30		✓	✓	✓	✓	✓	
10:30 - 11:00		✓	✓	✓	✓	✓	
11:00 - 11:30		✓	✓	✓	✓	✓	
11:30 - 12:00		✓	✓	✓	✓	✓	
12:00 - 12:30		✓	✓	✓	✓	✓	
12:30 - 13:00		✓	✓	✓	✓	✓	
13:00 - 13:30		✓	✓	✓	✓	✓	
13:30 - 14:00		✓	✓	✓	✓	✓	
14:00 - 14:30		✓	✓	✓	✓	✓	
14:30 - 15:00		✓	✓	✓	✓	✓	
15:00 - 15:30		✓	✓	✓	✓	✓	
15:30 - 16:00		✓	✓	✓	✓	✓	
16:00 - 16:30		✓	✓	✓	✓	✓	
16:30 - 17:00		✓	✓	✓	✓	✓	
17:00 - 17:30		✓	✓	✓	✓	✓	
17:30 - 18:00		✓	✓	✓	✓	✓	

*Tommy Law*  
*10/28/17*

Verified by Tommy Law (ES) \_\_\_\_\_  
 Date 10/10/17

KL 7286

# 地盆水車灑水記錄表(2017)

	星期日	星期一	星期二	星期三	星期四	星期五	星期六
	10月22日	10月23日	10月24日	10月25日	10月26日	10月27日	10月28日
8:00 - 8:30		✓	✓	✓	✓	✓	
8:30 - 9:00		✓	✓	✓	✓	✓	
9:00 - 9:30		✓	✓	✓	✓	✓	
9:30 - 10:00		✓	✓	✓	✓	✓	
10:00 - 10:30		✓	✓	✓	✓	✓	
10:30 - 11:00		✓	✓	✓	✓	✓	
11:00 - 11:30		✓	✓	✓	✓	✓	
11:30 - 12:00		✓	✓	✓	✓	✓	
12:00 - 12:30		✓	✓	✓	✓	✓	
12:30 - 13:00		✓	✓	✓	✓	✓	
13:00 - 13:30		✓	✓	✓	✓	✓	
13:30 - 14:00		✓	✓	✓	✓	✓	
14:00 - 14:30		✓	✓	✓	✓	✓	
14:30 - 15:00		✓	✓	✓	✓	✓	
15:00 - 15:30		✓	✓	✓	✓	✓	
15:30 - 16:00		✓	✓	✓	✓	✓	
16:00 - 16:30		✓	✓	✓	✓	✓	
16:30 - 17:00		✓	✓	✓	✓	✓	
17:00 - 17:30		✓	✓	✓	✓	✓	
17:30 - 18:00		✓	✓	✓	✓	✓	

Lai kam Yee    Lai kam Tin    Lai kam Tin    Lai kam Tin    Lai kam Tin    Lai kam Tin    Lai kam Tin


Verified by Tommy Law (ES)  
 Date 30/10/2017

HC 857

# 地盆水車灑水記錄表(2017)

	星期日	星期一	星期二	星期三	星期四	星期五	星期六
	10月22日	10月23日	10月24日	10月25日	10月26日	10月27日	10月28日
8:00 - 8:30		✓	✓	✓	✓	✓	
8:30 - 9:00		✓	✓	✓	✓	✓	
9:00 - 9:30		✓	✓	✓	✓	✓	
9:30 - 10:00		✓	✓	✓	✓	✓	
10:00 - 10:30		✓	✓	✓	✓	✓	
10:30 - 11:00		✓	✓	✓	✓	✓	
11:00 - 11:30		✓	✓	✓	✓	✓	
11:30 - 12:00		✓	✓	✓	✓	✓	
12:00 - 12:30		✓	✓	✓	✓	✓	
12:30 - 13:00		✓	✓	✓	✓	✓	
13:00 - 13:30		✓	✓	✓	✓	✓	
13:30 - 14:00		✓	✓	✓	✓	✓	
14:00 - 14:30		✓	✓	✓	✓	✓	
14:30 - 15:00		✓	✓	✓	✓	✓	
15:00 - 15:30		✓	✓	✓	✓	✓	
15:30 - 16:00		✓	✓	✓	✓	✓	
16:00 - 16:30		✓	✓	✓	✓	✓	
16:30 - 17:00		✓	✓	✓	✓	✓	
17:00 - 17:30		✓	✓	✓	✓	✓	
17:30 - 18:00		✓	✓	✓	✓	✓	

蔡 真 榮 榮 榮

  
 Verified by Tommy Law (ES)  
 Date 30/10/2017

**Contract No. HY/2013/12**  
**Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works**

**Investigation Report on Action or Limit Level Non-compliance**

<b>Date</b>	2 November 2017		
<b>Environmental Aspect</b>	Air Quality		
<b>Parameter</b>	1-hour TSP		
<b>Monitoring Location</b>	ASR5 (Pillar Point Fire Station)	ASR10 (Butterfly Beach Park)	
<b>Measurement Period</b>	13:08-14:08	12:45-13:45	15:35-16:35
<b>Action Level (ug/m<sup>3</sup>)</b>	340	337	337
<b>Limit Level (ug/m<sup>3</sup>)</b>	500	500	500
<b>Measured Level (ug/m<sup>3</sup>)</b>	<b>351</b>	<b>403</b>	<b>816</b>
<b>Exceedance</b>	<b>Action Level</b>	<b>Action Level</b>	<b>Limit Level</b>
<b>Possible reason for Action or Limit Level Non-compliance</b>	<ol style="list-style-type: none"> <li>1. According to site information provided by CRBC-Kaden JV, road and drainage works at Platform 19 and Slope 170, construction of bus shelter at Retaining Wall B, housekeeping works at Lung Mun Road and Butterfly Beach, road pavement works at East Portal and construction of column at Portion F were conducted on 2 November 2017.</li> <li>2. To reduce dust impact arising from the construction, mitigation measures for construction dust control were implemented. They include the followings:- <ul style="list-style-type: none"> <li>• water trucks were arranged on haul road to keep road surface wet (refer to photo 1, 12, 13 and water spraying record)</li> <li>• for un-accessible area, water spraying by workers was provided (refer to photo 2, 7, 8 and water spraying record)</li> <li>• Hydro seeding or covered part of the exposed slopes and stockpile by tarpaulin sheet (refer to Photo 3 to 5)</li> <li>• to set speed control at 8 km/hr for all vehicles using the haul road (refer to photo 6 and 9)</li> </ul> </li> <li>3. During the monitoring on 2 November 2017, it was observed that construction works was undertaken at the public toilet inside the Butterfly Beach Park which located near the ASR10 within 10m and not under the contract HY/2013/12. Therefore we considered that the exceedances at ASR10 are due to the construction works at the public toilet. (Ref. to Photo 19 &amp; 20)</li> <li>4. For the exceedance at ASR5, reviewing the data of the weather station setting up at ASR5 under Contract No. HY/2012/08, south-westerly wind at 1.3 to 1.8 m/s was blowing between 13:00 to 14:00. The monitoring station ASR5 was located at the upstream of the construction area.</li> <li>5. Also the works area Portion F which is closely to ASR5, only construction of column which include mobilize materials and installing metal formworks was undertaken in that area and most site area at Portion F was hard paved which is unlikely to create heavy construction dust impact. (Ref. to Location Plan and Photo 14 &amp; 18)</li> </ol>		

	<p>6. During the weekly site inspection on 31 October &amp; 7 November 2017, ET was observed that the contractor was properly implemented the dust mitigation measure under EMIS requirement at Portion F. (Ref. to Photo 7 &amp; 8) Therefore we considered that the cause of exceedances at ASR10 are due to the construction works at public toilet near the monitoring station; For the exceedance at ASR5 is due to other pollutant source rather than the construction site.</p> <p>7. Based on above investigation, the exceedance is unlikely related to the Contract work and no corrective action was required accordingly.</p>
<b>Action to be taken</b>	ET will continue regular audit and inspection for the implemented dust mitigation measures during the construction period.

**Prepared By :** T.W. Tam

**Designation :** Environmental Team Leader

**Signature :** 

**Date :** 4 December 2017

**Photo Record**



**Photo 1** Watering of haul road by water truck to keep road surface wet



**Photo 2** Water spraying by worker for un-accessible area.



**Photo 3** Covered part of the exposed slopes and stockpile by tarpaulin sheet.



**Photo 4** Hydro seeding for the exposed slope at slop 170



**Photo 5** Covered part of the exposed slopes and stockpile by tarpaulin sheet.



**Photo 6** Set speed control at ~8km/hr for all vehicles using the haul road





**Photo 7** Watering of haul road to keep road surface wet was observed at Portion F during the site inspection on 31 October 2017



**Photo 8** Watering of haul road to keep road surface wet was observed at Portion F during the site inspection on 7 November 2017



**Photo 9** Set speed control at ~8km/hr for all vehicles using the haul road at Portion F



**Photo 10** No dust emitted for the Portion F was observed during the site inspection on 31 October 2017 and the works area was clean and tidy



**Photo 11** No dust emitted for the Portion F was observed during the site inspection on 7 November 2017 and the works area was clean and tidy



**Photo 12** Watering of haul road by water truck to keep road surface wet was observed during the site inspection on 31 October 2017



**Photo 13** Two water truck were in operation during the site inspection on 31 October 2017



**Photo 14** Construction of column at Portion F and most works area was hard paved.



**Photo 15** Construction of bus shelter at Retaining Wall B.



**Photo 16** Drainage works at Platform 19



**Photo 17** Housekeeping works at Lung Mun Road.



**Photo 18** Construction of column at Portion F



**Photo 19** Construction works was undertaken near the ASR10



**Photo 20** Construction works was undertaken near the ASR10

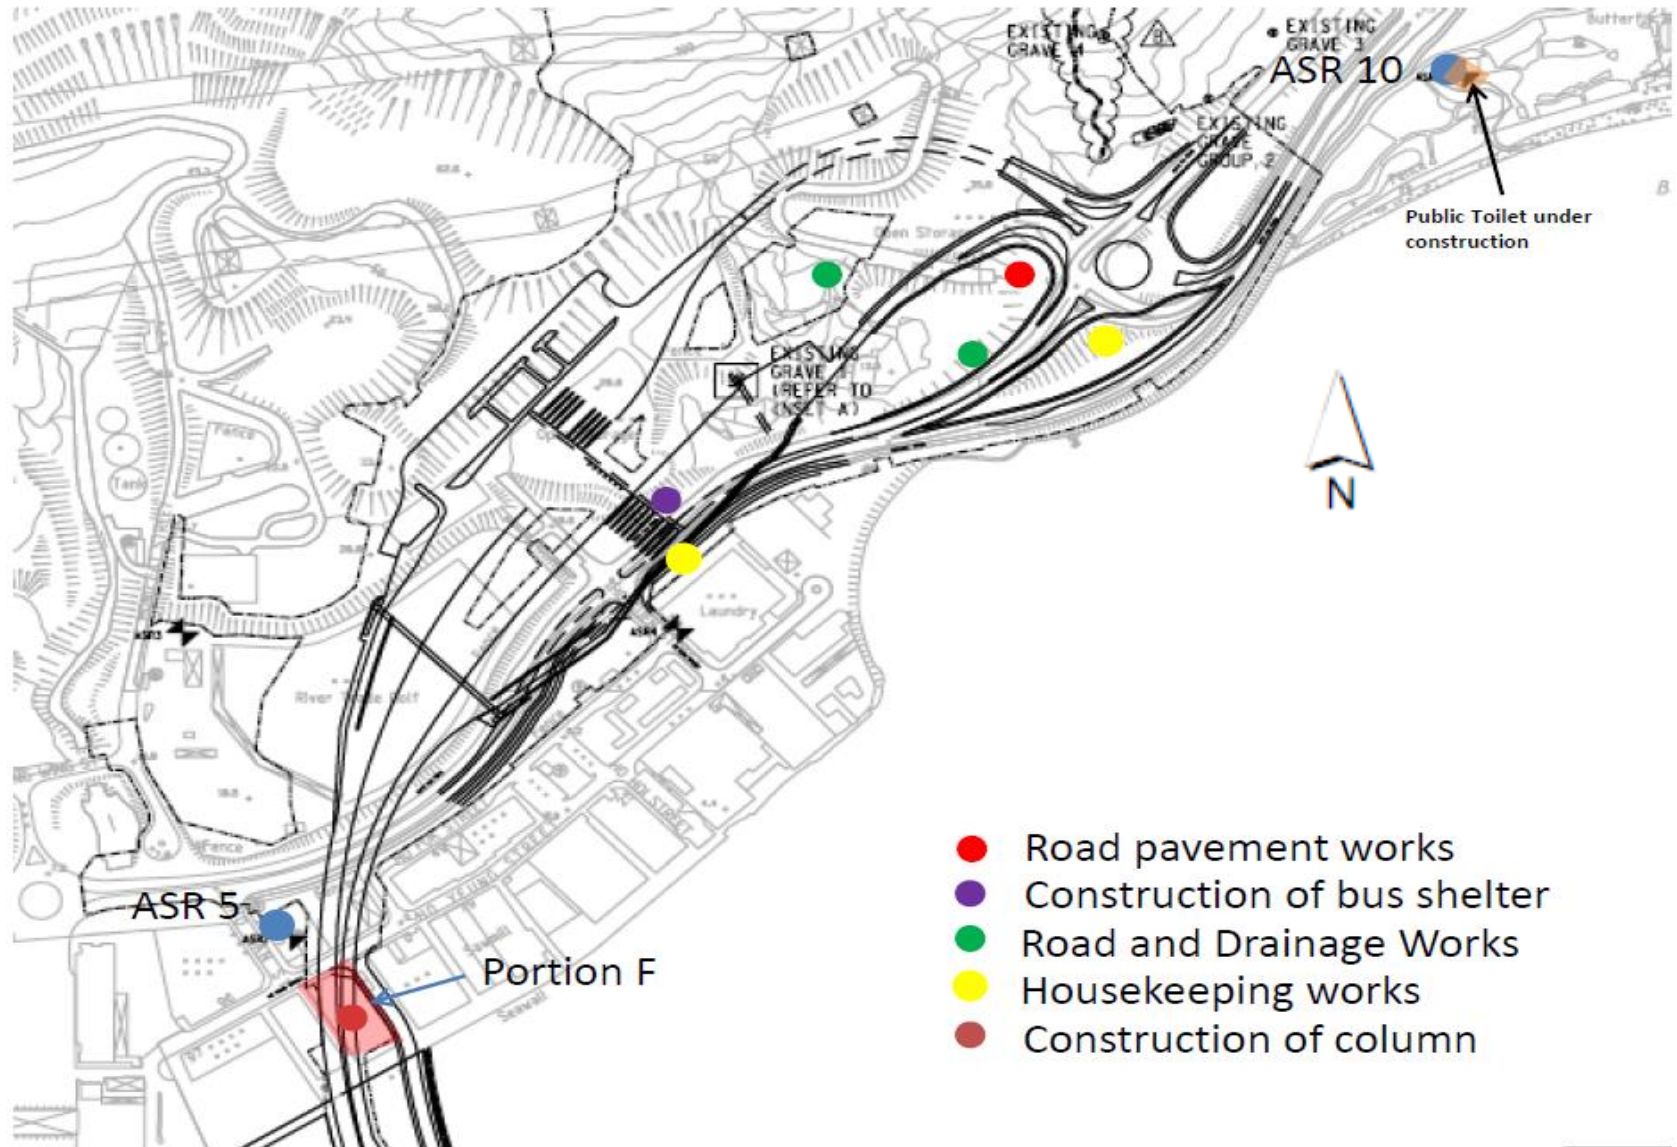


Figure 1. Location Plan

**Table 1. 1-Hr TSP Monitoring Result of 2 November 2017**

TMCLKL	HY/2012/08	2/11/2017	AQMS1	Sunny	13:30	1-hour TSP	259	ug/m3
TMCLKL	HY/2012/08	2/11/2017	AQMS1	Sunny	15:22	1-hour TSP	209	ug/m3
TMCLKL	HY/2012/08	2/11/2017	AQMS1	Sunny	16:24	1-hour TSP	158	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR1	Sunny	13:19	1-hour TSP	221	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR1	Sunny	15:10	1-hour TSP	214	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR1	Sunny	16:12	1-hour TSP	215	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR10	Sunny	12:45	1-hour TSP	403	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR10	Sunny	14:35	1-hour TSP	169	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR10	Sunny	15:35	1-hour TSP	816	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR5	Sunny	13:08	1-hour TSP	351	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR5	Sunny	14:59	1-hour TSP	315	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR5	Sunny	16:01	1-hour TSP	290	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR6	Sunny	12:57	1-hour TSP	267	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR6	Sunny	14:47	1-hour TSP	264	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR6	Sunny	15:49	1-hour TSP	248	ug/m3
TMCLKL	HY/2012/08	2/11/2017	AQMS1	Sunny	17:26	24-hour TSP	207	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR1	Sunny	17:14	24-hour TSP	203	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR10	Sunny	16:39	24-hour TSP	188	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR5	Sunny	17:03	24-hour TSP	222	ug/m3
TMCLKL	HY/2012/08	2/11/2017	ASR6	Sunny	16:51	24-hour TSP	150	ug/m3

**Table 2. Wind Direction and Speed data during 1-Hr TSP Monitoring**

Date	Time	Average of Wind Speed (m/s)	Average of Wind Direction (degree)
2/11/2017	13:00	1.8	231
2/11/2017	14:00	1.3	225
2/11/2017	15:00	1.3	226
2/11/2017	16:00	1.8	230

**Remarks:**

Wind speed and direction data was extracted from the weather station located at ASR5 set up by ET of Contract HY/2012/08

# 地盆人手灑水記錄表(2017)

地點:	星期日	星期一	星期二	星期三	星期四	星期五	星期六
<i>On-Top</i>	10月29日	10月30日	10月31日	11月1日	11月2日	11月3日	11月4日
<i>On-Down</i>							
8:00 - 8:30	✓	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓	✓

u u u u u u u

Verified by Tommy Law (ES) [Signature]  
 Date 6/11/2018

# 地盆人手灑水記錄表(2017)

地點:	星期日	星期一	星期二	星期三	星期四	星期五	星期六
Slope Area.	10月29日	10月30日	10月31日	11月1日	11月2日	11月3日	11月4日
8:00 - 8:30		✓	✓	✓	✓	✓	✓
8:30 - 9:00		✓	✓	✓	✓	✓	✓
9:00 - 9:30		✓	✓	✓	✓	✓	✓
9:30 - 10:00		✓	✓	✓	✓	✓	✓
10:00 - 10:30		✓	✓	✓	✓	✓	✓
10:30 - 11:00		✓	✓	✓	✓	✓	✓
11:00 - 11:30		✓	✓	✓	✓	✓	✓
11:30 - 12:00		✓	✓	✓	✓	✓	✓
12:00 - 12:30		✓	✓	✓	✓	✓	✓
12:30 - 13:00		✓	✓	✓	✓	✓	✓
13:00 - 13:30		✓	✓	✓	✓	✓	✓
13:30 - 14:00		✓	✓	✓	✓	✓	✓
14:00 - 14:30		✓	✓	✓	✓	✓	✓
14:30 - 15:00		✓	✓	✓	✓	✓	✓
15:00 - 15:30		✓	✓	✓	✓	✓	✓
15:30 - 16:00		✓	✓	✓	✓	✓	✓
16:00 - 16:30		✓	✓	✓	✓	✓	✓
16:30 - 17:00		✓	✓	✓	✓	✓	✓
17:00 - 17:30		✓	✓	✓	✓	✓	✓
17:30 - 18:00		✓	✓	✓	✓	✓	✓

✓
✓
✓
✓
✓
✓
✓
✓

Verified by Tommy Law (ES) 6/11/2017  
 Date

# 地盆人手灑水記錄表(2017)

星期日	星期一	星期二	星期三	星期四	星期五	星期六
10月29日	10月30日	10月31日	11月1日	11月2日	11月3日	11月4日
地點: <i>Rocky</i>						
8:00 - 8:30	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓

*Tommy Law*

Verified by Tommy Law (ES) *TL*  
 Date 6/11/2017




WA 8376

# 地盆水車灑水記錄表(2017)

星期日	星期一	星期二	星期三	星期四	星期五	星期六
10月29日	10月30日	10月31日	11月1日	11月2日	11月3日	11月4日
8:00 - 8:30	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓

梁 梁 梁 梁 梁 梁 梁

Verified by Tommy Law (ES)   
 Date 6/11/10A

NL7286

# 地盆水車灑水記錄表(2017)

星期日	星期一	星期二	星期三	星期四	星期五	星期六
10月29日	10月30日	10月31日	11月1日	11月2日	11月3日	11月4日
8:00 - 8:30	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓

Lai Kam Yin      Loi Kam Yau      Loi Kam Yin      Kai Kwan      Loi Kam Yin      Loi Kam Yin

Verified by Tommy Law (ES)

Date

  
6/11/2017

**Contract No. HY/2013/12**  
**Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works**


**Investigation Report on Action or Limit Level Non-compliance**

<b>Date</b>	11 November 2017
<b>Environmental Aspect</b>	Air Quality
<b>Parameter</b>	1-hour TSP
<b>Monitoring Location</b>	ASR5 (Pillar Point Fire Station)
<b>Measurement Period</b>	8:45-9:45
<b>Action Level (ug/m3)</b>	340
<b>Limit Level (ug/m3)</b>	500
<b>Measured Level (ug/m3)</b>	389
<b>Exceedance</b>	<b>Action Level</b>
<b>Possible reason for Action or Limit Level Non-compliance</b>	<ol style="list-style-type: none"> <li>1. According to site information provided by CRBC-Kaden JV, road and drainage works at Platform 19 and Bridge G1, construction of footbridge at Retaining Wall F, housekeeping works at Lung Mun Road and Butterfly Beach, road pavement works at East Portal and construction of column at Portion F were conducted on 11 November 2017.</li> <li>2. To reduce dust impact arising from the construction, mitigation measures for construction dust control were implemented. They include the followings:- <ul style="list-style-type: none"> <li>• water trucks were arranged on haul road to keep road surface wet (refer to photo 1 and water spraying record)</li> <li>• for un-accessible area such as the works area that water truck cannot access, water spraying by workers was provided (refer to photo 2, 7, 8 and water spraying record)</li> <li>• Hydro seeding or covered part of the exposed slopes and stockpile by tarpaulin sheet (refer to Photo 3 to 5)</li> <li>• to set speed control at 8 km/hr for all vehicles using the haul road (refer to photo 6 and 9)</li> </ul> </li> <li>3. During site inspection on 7 &amp; 14 November 2017, it was observed that the dust mitigation measures were implemented and the site condition is acceptable. Photo showing the implemented dust mitigation measures on 7 &amp; 14 November 2017 is shown in photo record.</li> <li>4. According to the weather station setting up at ASR5 under Contract No. HY/2012/08, east wind at 2.2 to 3.1 m/s was blowing between 8:00 to 10:00. Review the monitoring result at other monitoring stations which was located more closely to the major site area no exceedance was recorded at similar time. Although the works area Portion F was located closely of the monitoring station ASR5, most of the site area at Portion F was hard paved and only consecution of column was undertaken on 11 November 2017. It is unlikely to create heavy construction dust impact. (Ref. to Location Plan and Photo 10, 11 &amp; 16) In addition, no further exceedances were recorded on the following monitoring days while similar site activities were carried on.</li> <li>5. Also the contractor was properly implemented the dust mitigation measure under EMIS requirement. Therefore we</li> </ol>

	<p>considered that the cause of exceedance is due to other pollutant source rather than the construction site.</p> <p>6. Based on above investigation, the exceedance is unlikely related to the Contract work and the exceedance is sporadic case. No corrective action was required accordingly.</p>
<b>Action to be taken</b>	ET will continue regular audit and inspection for the implemented dust mitigation measures during the construction period.

**Prepared By :** T.W. Tam

**Designation :** Environmental Team Leader

**Signature :**   
\_\_\_\_\_

**Date :** 4 December 2017

**Photo Record**



**Photo 1** Watering of haul road by water truck to keep road surface wet



**Photo 2** Water spraying by worker for un-accessible area.



**Photo 3** Covered part of the exposed slopes and stockpile by tarpaulin sheet.



**Photo 4** Hydro seeding for the exposed slope at slop 170



**Photo 5** Covered part of the exposed slopes and stockpile by tarpaulin sheet.



**Photo 6** Set speed control at ~8km/hr for all vehicles using the haul road



**Photo 7** Watering of haul road to keep road surface wet was observed at Portion F during the site inspection on 7 November 2017



**Photo 8** Watering of haul road to keep road surface wet was observed at Portion F during the site inspection on 14 November 2017



**Photo 9** Set speed control at ~8km/hr for all vehicles using the haul road at Portion F




**Photo 10** No dust emitted for the Portion F was observed during the site inspection on 7 November 2017 and the works area was clean and tidy



**Photo 11** No dust emitted for the Portion F was observed during the site inspection on 14 November 2017 and the works area was clean and tidy



**Photo 12** Construction of bus shelter at Retaining Wall F

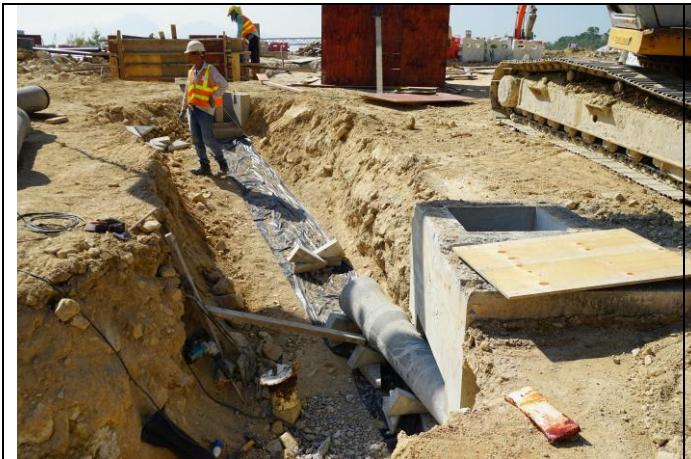

**Photo 13** Drainage works at Platform 19



**Photo 14** Housekeeping works at Lung Mun Road.



**Photo 15** Housekeeping works at Butterfly Beach



**Photo 16** Construction of column at Portion F

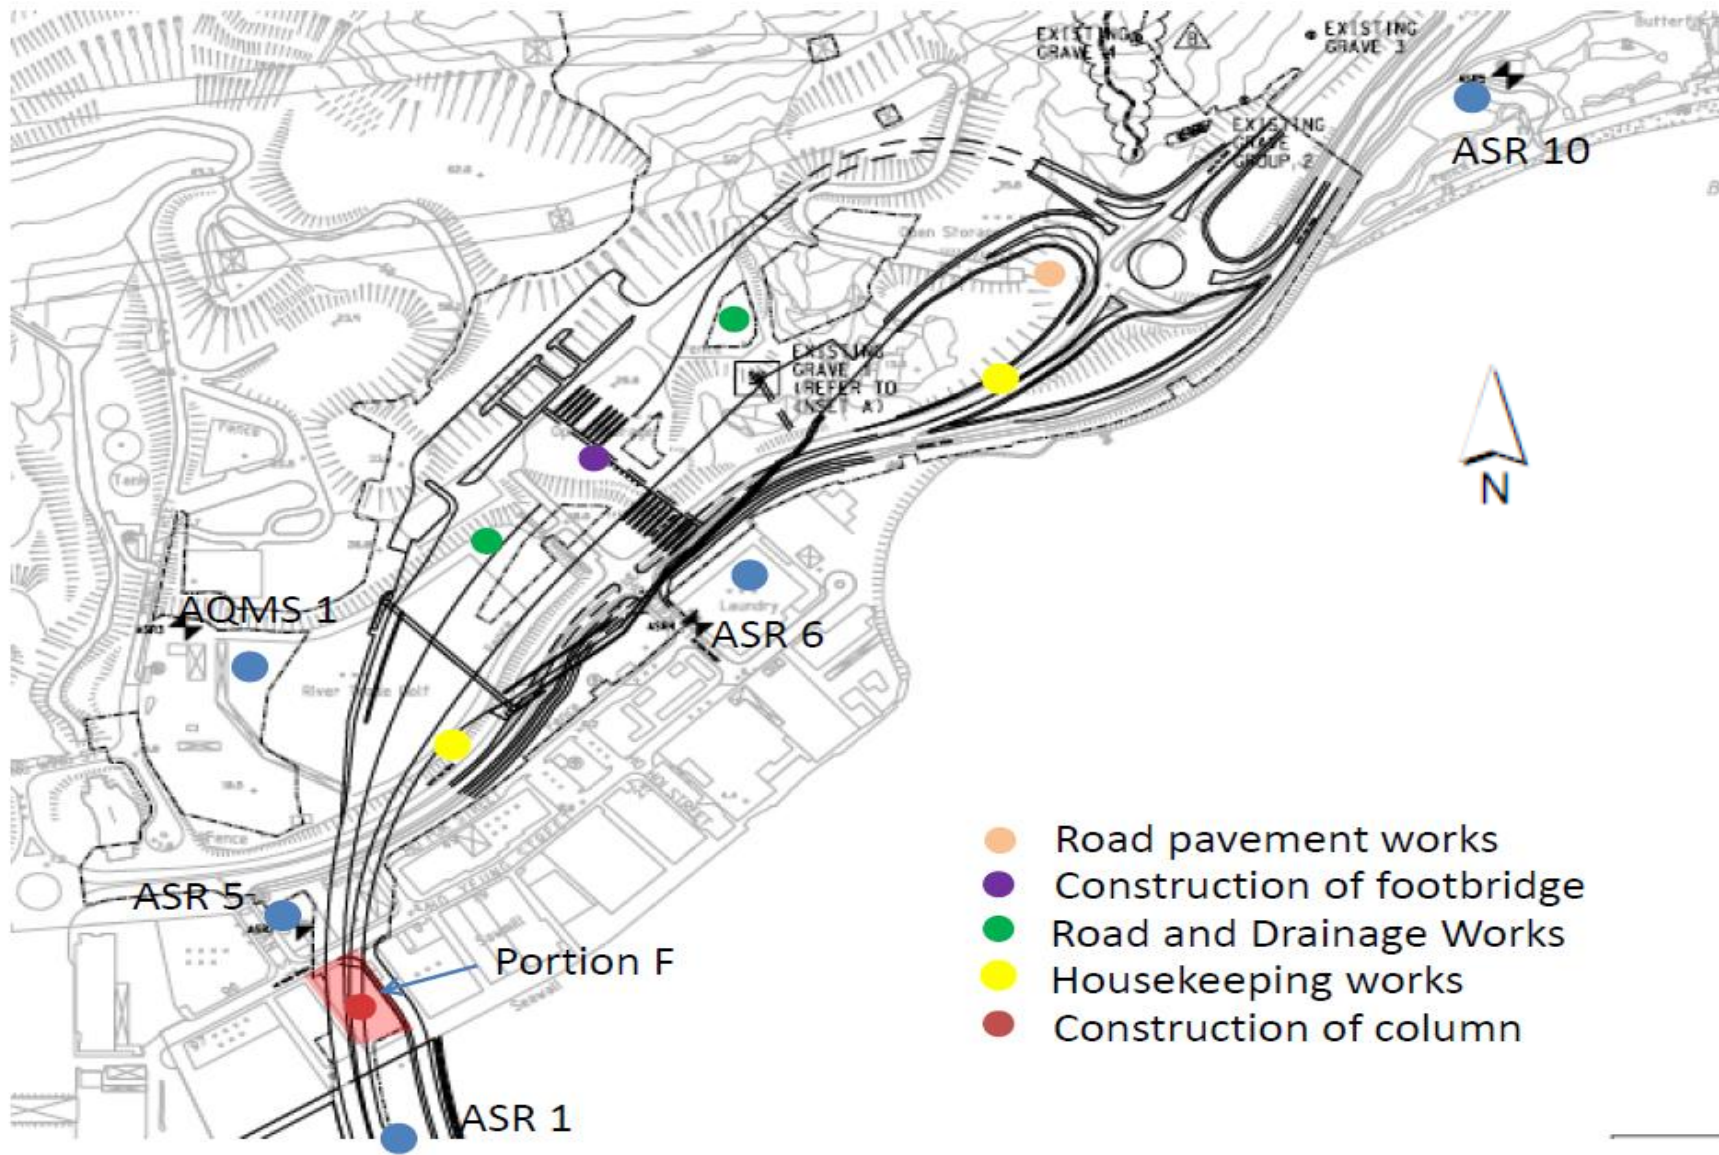


Figure 1. Location Plan



**Table 1. 1-Hr TSP Monitoring Result of 11 November 2017**

TMCLKL	HY/2012/08	11/11/2017	AQMS1	Sunny	9:08	1-hour TSP	163	ug/m3
TMCLKL	HY/2012/08	11/11/2017	AQMS1	Sunny	10:10	1-hour TSP	131	ug/m3
TMCLKL	HY/2012/08	11/11/2017	AQMS1	Sunny	11:12	1-hour TSP	138	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR1	Sunny	8:56	1-hour TSP	251	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR1	Sunny	9:58	1-hour TSP	161	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR1	Sunny	11:00	1-hour TSP	195	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR10	Sunny	8:22	1-hour TSP	141	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR10	Sunny	9:24	1-hour TSP	109	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR10	Sunny	10:16	1-hour TSP	123	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR5	Sunny	8:45	1-hour TSP	389	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR5	Sunny	9:47	1-hour TSP	196	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR5	Sunny	10:49	1-hour TSP	217	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR6	Sunny	8:33	1-hour TSP	236	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR6	Sunny	9:35	1-hour TSP	172	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR6	Sunny	10:37	1-hour TSP	146	ug/m3
TMCLKL	HY/2012/08	11/11/2017	AQMS1	Sunny	12:14	24-hour TSP	78	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR1	Sunny	12:02	24-hour TSP	106	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR10	Sunny	11:28	24-hour TSP	71	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR5	Sunny	11:51	24-hour TSP	103	ug/m3
TMCLKL	HY/2012/08	11/11/2017	ASR6	Sunny	11:39	24-hour TSP	98	ug/m3

**Table 2. Wind Direction and Speed data during 1-Hr TSP Monitoring**

Date	Time	Average of Wind Speed (m/s)	Average of Wind Direction (degree)
11/11/2017	8:00	3.1	92
11/11/2017	9:00	2.2	84
11/11/2017	10:00	3.1	86

**Remarks:**

Wind speed and direction data was extracted from the weather station located at ASR5 set up by ET of Contract HY/2012/08

# 地盆人手灑水記錄表(2017)

星期日	星期一	星期二	星期三	星期四	星期五	星期六
11月5日	11月6日	11月7日	11月8日	11月9日	11月10日	11月11日
地點: <i>Slope Area</i>						
8:00 - 8:30	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓








Verified by Tommy Law (ES)

Date 13/11/2017

# 地盆人手灑水記錄表(2017)





地點: <i>Casdy Div. Ser.</i>	星期日	星期一	星期二	星期三	星期四	星期五	星期六
	11月5日	11月6日	11月7日	11月8日	11月9日	11月10日	11月11日
8:00 - 8:30		✓	✓	✓	✓	✓	✓
8:30 - 9:00		✓	✓	✓	✓	✓	✓
9:00 - 9:30		✓	✓	✓	✓	✓	✓
9:30 - 10:00		✓	✓	✓	✓	✓	✓
10:00 - 10:30		✓	✓	✓	✓	✓	✓
10:30 - 11:00		✓	✓	✓	✓	✓	✓
11:00 - 11:30		✓	✓	✓	✓	✓	✓
11:30 - 12:00		✓	✓	✓	✓	✓	✓
12:00 - 12:30		✓	✓	✓	✓	✓	✓
12:30 - 13:00		✓	✓	✓	✓	✓	✓
13:00 - 13:30		✓	✓	✓	✓	✓	✓
13:30 - 14:00		✓	✓	✓	✓	✓	✓
14:00 - 14:30		✓	✓	✓	✓	✓	✓
14:30 - 15:00		✓	✓	✓	✓	✓	✓
15:00 - 15:30		✓	✓	✓	✓	✓	✓
15:30 - 16:00		✓	✓	✓	✓	✓	✓
16:00 - 16:30		✓	✓	✓	✓	✓	✓
16:30 - 17:00		✓	✓	✓	✓	✓	✓
17:00 - 17:30		✓	✓	✓	✓	✓	✓
17:30 - 18:00		✓	✓	✓	✓	✓	✓


*Handwritten signature*

Verified by Tommy Law (ES) \_\_\_\_\_  
 Date 13/11/2017

# 地盆人手灑水記錄表(2017)

星期日	星期一	星期二	星期三	星期四	星期五	星期六
11月5日	11月6日	11月7日	11月8日	11月9日	11月10日	11月11日
8:00 - 8:30	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓


Verified by Tommy Law (ES)   
 Date 13/11/2017

667226

# 地盆水車灑水記錄表(2017)

	星期日	星期一	星期二	星期三	星期四	星期五	星期六
	11月5日	11月6日	11月7日	11月8日	11月9日	11月10日	11月11日
8:00 - 8:30	✓	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓	✓

Lai Kam Tin Lai Kam Tin Lai Kam Tin Lai Kam Tin Lai Kam Tin Lai Kam Tin Lai Kam Tin


Verified by Tommy Law (ES)  
 Date 03/11/17

WA 2376

# 地盆水車灑水記錄表(2017)

星期日	星期一	星期二	星期三	星期四	星期五	星期六
11月5日	11月6日	11月7日	11月8日	11月9日	11月10日	11月11日
8:00 - 8:30	✓	✓	✓	✓	✓	✓
8:30 - 9:00	✓	✓	✓	✓	✓	✓
9:00 - 9:30	✓	✓	✓	✓	✓	✓
9:30 - 10:00	✓	✓	✓	✓	✓	✓
10:00 - 10:30	✓	✓	✓	✓	✓	✓
10:30 - 11:00	✓	✓	✓	✓	✓	✓
11:00 - 11:30	✓	✓	✓	✓	✓	✓
11:30 - 12:00	✓	✓	✓	✓	✓	✓
12:00 - 12:30	✓	✓	✓	✓	✓	✓
12:30 - 13:00	✓	✓	✓	✓	✓	✓
13:00 - 13:30	✓	✓	✓	✓	✓	✓
13:30 - 14:00	✓	✓	✓	✓	✓	✓
14:00 - 14:30	✓	✓	✓	✓	✓	✓
14:30 - 15:00	✓	✓	✓	✓	✓	✓
15:00 - 15:30	✓	✓	✓	✓	✓	✓
15:30 - 16:00	✓	✓	✓	✓	✓	✓
16:00 - 16:30	✓	✓	✓	✓	✓	✓
16:30 - 17:00	✓	✓	✓	✓	✓	✓
17:00 - 17:30	✓	✓	✓	✓	✓	✓
17:30 - 18:00	✓	✓	✓	✓	✓	✓

梁 泉 梁 泉 梁 泉 梁 泉

Verified by Tommy Law (ES)   
 Date 13/11/2018

## **Appendix K**

### **Checklist for Landscape and Visual Monitoring**

Contract No. HY/2013/12

Tuen Mun – Chek Lap Kok Link – Northern Connection Toll Plaza and Associated Works



中國路橋  
CRBC



**Landscape and Visual Checklist**

**Monitoring Date: 03<sup>rd</sup> November 2017**


Item	Environmental Protection Measures	Location/ Timing	Implementation Agent	Status				Remarks
				A	UA	IR	NA	
1	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage)	All areas / During construction	Design Consultant/ Contractor	√				
2	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme	All areas / During construction	Design Consultant/ Contractor	√				Tree Transplanting works conducted on 22-May-17.
3	Hillside and roadside screen planting to proposed roads, associated structures and slope works	All areas / During construction	Design Consultant/ Contractor				√	Construction of roads planting not commenced yet
4	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone)	All areas / During construction	Design Consultant/ Contractor				√	No stockpile in the reporting period
5	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works	All areas / During construction	Design Consultant/ Contractor				√	For some area, erection of hoarding was not feasible due to the limitation of





								traffic sight line; water barrier with panel was used to screen works.
6	Control night-time lighting and glare by hooding all lights	All areas / During construction	Design Consultant/ Contractor	√				Only temporary traffic management lighting was applied.
7	Ensure no run-off into water body adjacent to the Project Area	All areas / During construction	Design Consultant/ Contractor	√				
8	Avoidance of excessive height and bulk of buildings and structures	All areas / During construction	Design Consultant/ Contractor				√	No high-rise building would be constructed.
9	Recycle/Reuse all felled trees and vegetation, e.g. mulching	All areas / During construction	Design Consultant/ Contractor				√	
10	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006	All areas / During construction	Design Consultant/ Contractor				√	Compensatory planting will be carry out in later stage of the project.

Legend: A=Acceptable, UA= Unacceptable, IR=Improvement Required, N/A=Not Applicable

Note: All item reference to Technical Memorandum on Environmental Impact Assessment, TM-CLKL EIA Section 10.9 & Project EM&A Manual Section 7.6

Checked and Monitored by:  Chung Koon Wah Albert (RLA) No. R-150 (Date) 4/12/2017

Checked by:  T. W. Tam (ET) 11 Dec 2017 (Date)

Checked by:  F. C. Tsang (IEC) 12/12/2017 (Date)  
(F. C. TSANG)



Item 1. Existing trees on boundary of the Project Area should be protected carefully during construction.



Item 2. Tree Transplanting works conducted on 22-May-17.



Item 5. Hoarding with panel around works area & Item 6. Temporary traffic management lighting.



Item 7. Ensure no run-off into water body.

Contract No. HY/2013/12

Tuen Mun – Chek Lap Kok Link – Northern Connection Toll Plaza and Associated Works



中國路橋  
CRBC



**Landscape and Visual Checklist**


**Monitoring Date: 10<sup>th</sup> November 2017**


Item	Environmental Protection Measures	Location/ Timing	Implementation Agent	Status				Remarks
				A	UA	IR	NA	
1	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage)	All areas / During construction	Design Consultant/ Contractor	√				
2	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme	All areas / During construction	Design Consultant/ Contractor	√				Tree Transplanting works conducted on 22-May-17.
3	Hillside and roadside screen planting to proposed roads, associated structures and slope works	All areas / During construction	Design Consultant/ Contractor				√	Construction of roads planting not commenced yet
4	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone)	All areas / During construction	Design Consultant/ Contractor				√	No stockpile in the reporting period
5	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works	All areas / During construction	Design Consultant/ Contractor				√	For some area, erection of hoarding was not feasible due to the limitation of


								traffic sight line; water barrier with panel was used to screen works.
6	Control night-time lighting and glare by hooding all lights	All areas / During construction	Design Consultant/ Contractor	√				Only temporary traffic management lighting was applied.
7	Ensure no run-off into water body adjacent to the Project Area	All areas / During construction	Design Consultant/ Contractor	√				
8	Avoidance of excessive height and bulk of buildings and structures	All areas / During construction	Design Consultant/ Contractor				√	No high-rise building would be constructed.
9	Recycle/Reuse all felled trees and vegetation, e.g. mulching	All areas / During construction	Design Consultant/ Contractor				√	
10	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006	All areas / During construction	Design Consultant/ Contractor				√	Compensatory planting will be carry out in later stage of the project.

Legend: A=Acceptable, UA= Unacceptable, IR=Improvement Required, N/A=Not Applicable

Note: All item reference to Technical Memorandum on Environmental Impact Assessment, TM-CLKL EIA Section 10.9 & Project EM&A Manual Section 7.6

Checked and Monitored by:  Chung Koon Wah Albert (RLA) No. R-150 (Date) 4/12/2017

Checked by:  T. W. Tam (ET) 11 Dec 2017 (Date)

Checked by:  F. C. Tsang (IEC) 12/12/2017 (Date)  
(F. C. TSANG)



Item 1. Existing trees on boundary of the Project Area should be protected carefully during construction.



Item 2. Tree Transplanting works conducted on 22-May-17.



Item 5. Hoarding with panel around works area & Item 6. Temporary traffic management lighting.



Item 7. Ensure no run-off into water body.

Contract No. HY/2013/12

Tuen Mun – Chek Lap Kok Link – Northern Connection Toll Plaza and Associated Works



中國路橋  
CRBC



基利

Landscape and Visual Checklist

Monitoring Date: 17<sup>th</sup> November 2017

Item	Environmental Protection Measures	Location/ Timing	Implementation Agent	Status				Remarks
				A	UA	IR	NA	
1	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage)	All areas / During construction	Design Consultant/ Contractor	√				
2	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme	All areas / During construction	Design Consultant/ Contractor	√				Tree Transplanting works conducted on 22-May-17.
3	Hillside and roadside screen planting to proposed roads, associated structures and slope works	All areas / During construction	Design Consultant/ Contractor				√	Construction of roads planting not commenced yet
4	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone)	All areas / During construction	Design Consultant/ Contractor				√	No stockpile in the reporting period
5	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works	All areas / During construction	Design Consultant/ Contractor				√	For some area, erection of hoarding was not feasible due to the limitation of





								traffic sight line; water barrier with panel was used to screen works.
6	Control night-time lighting and glare by hooding all lights	All areas / During construction	Design Consultant/ Contractor	√				Only temporary traffic management lighting was applied.
7	Ensure no run-off into water body adjacent to the Project Area	All areas / During construction	Design Consultant/ Contractor	√				
8	Avoidance of excessive height and bulk of buildings and structures	All areas / During construction	Design Consultant/ Contractor				√	No high-rise building would be constructed.
9	Recycle/Reuse all felled trees and vegetation, e.g. mulching	All areas / During construction	Design Consultant/ Contractor				√	
10	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006	All areas / During construction	Design Consultant/ Contractor				√	Compensatory planting will be carry out in later stage of the project.

Legend: A=Acceptable, UA= Unacceptable, IR=Improvement Required, N/A=Not Applicable

Note: All item reference to Technical Memorandum on Environmental Impact Assessment, TM-CLKL EIA Section 10.9 & Project EM&A Manual Section 7.6

Checked and Monitored by:  **Chung Koon Wah Albert** (RLA) No. R-150 (Date) 4/12/2017

Checked by:  **T. W. Tam** (ET) 11 Dec 2017 (Date)

Checked by:  **F. C. TSANG** (IEC) 12/12/2017 (Date)



Item 1. Existing trees on boundary of the Project Area should be protected carefully during construction.



Item 2. Tree Transplanting works conducted on 22-May-17.



Item 5. Hoarding with panel around works area & Item 6. Temporary traffic management lighting.



Item 7. Ensure no run-off into water body.

Contract No. HY/2013/12

Tuen Mun – Chek Lap Kok Link – Northern Connection Toll Plaza and Associated Works



中國路橋  
CRBC



Landscape and Visual Checklist


**Monitoring Date: 24<sup>th</sup> November 2017**


Item	Environmental Protection Measures	Location/ Timing	Implementation Agent	Status				Remarks
				A	UA	IR	NA	
1	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage)	All areas / During construction	Design Consultant/ Contractor	√				
2	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme	All areas / During construction	Design Consultant/ Contractor	√				Tree Transplanting works conducted on 22-May-17.
3	Hillside and roadside screen planting to proposed roads, associated structures and slope works	All areas / During construction	Design Consultant/ Contractor				√	Construction of roads planting not commenced yet
4	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone)	All areas / During construction	Design Consultant/ Contractor				√	No stockpile in the reporting period
5	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works	All areas / During construction	Design Consultant/ Contractor				√	For some area, erection of hoarding was not feasible due to the limitation of


								traffic sight line; water barrier with panel was used to screen works.
6	Control night-time lighting and glare by hooding all lights	All areas / During construction	Design Consultant/ Contractor	√				Only temporary traffic management lighting was applied.
7	Ensure no run-off into water body adjacent to the Project Area	All areas / During construction	Design Consultant/ Contractor	√				
8	Avoidance of excessive height and bulk of buildings and structures	All areas / During construction	Design Consultant/ Contractor				√	No high-rise building would be constructed.
9	Recycle/Reuse all felled trees and vegetation, e.g. mulching	All areas / During construction	Design Consultant/ Contractor				√	
10	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006	All areas / During construction	Design Consultant/ Contractor				√	Compensatory planting will be carry out in later stage of the project.

Legend: A=Acceptable, UA= Unacceptable, IR=Improvement Required, N/A=Not Applicable

Note: All item reference to Technical Memorandum on Environmental Impact Assessment, TM-CLKL EIA Section 10.9 & Project EM&A Manual Section 7.6

Checked and Monitored by:  **Chung Koon Wah Albert (RLA) No. R-150 (Date) 4/12/2017**

Checked by:  **Tia Tam (ET) 11 Dec 2017 (Date)**

Checked by:  **F. C. TSANG (IEC) 12/12/2017 (Date)**



Item 1. Existing trees on boundary of the Project Area should be protected carefully during construction.



Item 2. Tree Transplanting works was conducted on 22-May-17.



Item 5. Hoarding with panel around works area & Item 6. Temporary traffic management lighting.



Item 7. Ensure no run-off into water body.

## **Appendix L**

### **Monthly Summary Waste Flow Table**



## Appendix A –Monthly Waste Flow Table

Monthly Summary Waste Flow Table for 2017 (year)

Month	Annual Quantities of Inert C&D Materials Generated Monthly						Annual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Concrete	Reused in the Contract	Reused in other Projects	Disposed as Public Fill	Imported Fill	Metals (see note 4)	Paper / cardboard packaging (see note 4)	Plastics & Rubber (see note 2)	Chemical Waste	Others (general refuse)
	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000m <sup>3</sup> )	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m <sup>3</sup> )
Jan	13.334	0.000	4.543	7.512	1.062	0.000	0.000	0.000	0.000	0.000	0.217
Feb	14.323	0.000	1.066	10.617	2.566	0.000	0.000	0.000	0.000	0.000	0.074
Mar	18.707	0.000	2.116	12.844	3.413	0.000	0.000	0.000	0.000	0.000	0.334
Apr	10.839	0.000	2.291	7.287	1.099	0.000	0.000	0.000	0.000	0.000	0.162
May	10.418	0.000	2.089	7.793	0.341	0.000	0.000	0.000	0.000	0.000	0.195
June	7.465	0.000	2.111	4.388	0.789	0.000	0.000	0.000	0.000	0.000	0.177
Sub-total	75.086	0.000	14.216	50.441	9.270	0.000	0.000	0.000	0.000	0.000	1.159
July	6.783	0.000	1.961	3.482	1.120	0.000	0.000	0.000	0.000	0.000	0.220
Aug	4.154	0.000	1.768	1.547	0.660	0.000	0.000	0.000	0.000	0.000	0.179
Sept	2.373	0.000	0.367	0.558	1.274	0.000	0.000	0.000	0.000	0.000	0.174
Oct	2.701	0.000	0.754	0.491	1.215	0.000	0.000	0.000	0.000	0.000	0.241
Nov	29.818	0.000	0.871	26.51	1.557	0.000	0.000	0.000	0.000	0.000	0.880
Dec											
Total	120.914	0.000	19.937	83.029	15.096	0.000	0.000	0.000	0.000	0.000	2.853

Notes:

- 1 The waste flow table shall also include C&D materials that are specified in the contract to be imported for use at the Site.
- 2 Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging materials.
- 3 Broken concrete for recycling into aggregates.

## **Appendix M**

### **Environmental Mitigation and Enhancement Measures Implementation Schedule (EMIS)**

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

Air Quality									
EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status *
						D	C	O	
4.8.1	3.8	An effective watering programme of twice daily watering with complete coverage, is estimated to reduce by 50%. This is recommended for all areas in order to reduce dust levels to a minimum;	All areas / throughout construction period	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		✓
4.8.1	3.8	Watering of the construction sites in Lantau for 8 times/day and in Tuen Mun for 12 times/day to reduce dust emissions by 87.5% and 91.7% respectively and shall be undertaken.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	The Contractor shall, to the satisfaction of the Engineer, install effective dust suppression measures and take such other measures as may be necessary to ensure that at the Site boundary and any nearby sensitive receiver, dust levels are kept to acceptable levels.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	The Contractor shall not burn debris or other materials on the works areas.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	In hot, dry or windy weather, the watering programme shall maintain all exposed road surfaces and dust sources wet.	All unpaved haul roads / throughout construction period in hot, dry or windy weather	Contractor	TMEIA Avoid smoke impacts and disturbance		Y		<>
4.8.1	3.8	Where breaking of oversize rock/concrete is required, watering shall be implemented to control dust. Water spray shall be used during the handling of fill material at the site and at active cuts, excavation and fill sites where dust is likely to be created.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		<>
4.8.1	3.8	Open dropping heights for excavated materials shall be controlled to a maximum height of 2m to minimise the fugitive dust arising from unloading.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

4.8.1	3.8	During transportation by truck, materials shall not be loaded to a level higher than the side and tail boards, and shall be dampened or covered before transport.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	Materials having the potential to create dust shall not be loaded to a level higher than the side and tail boards, and shall be covered by a clean tarpaulin. The tarpaulin shall be properly secured and shall extend at least 300mm over the edges of the side and tail boards.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	No earth, mud, debris, dust and the like shall be deposited on public roads. Wheel washing facility shall be usable prior to any earthworks excavation activity on the site.	construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	Areas of exposed soil shall be minimized to areas in which works have been completed shall be restored as soon as is practicable.	All exposed surfaces / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.8.1	3.8	All stockpiles of aggregate or spoil shall be enclosed or covered and water applied in dry or windy condition.	All areas / throughout construction period	Contractor	TMEIA Avoid dust generation		Y		✓
4.11	Section 3	EM&A in the form of 1 hour and 24 hour dust monitoring and site audit	All representative existing ASRs / throughout construction period	Contractor	EM&A Manual		Y		✓

**Cultural Heritage**

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	
11.8	Section 9	EM&A in the form of audit of the mitigation measures	All areas / throughout construction period	Highways Department	EIAO-TM		Y		✓

**Ecology**

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

7.13#	6.3, 6.5#	Fencing or other physical barriers for protection of Pitcher Plant around Zones 8, 9 and 10 and the temporary nursery site	Tuen Mun Area 46 shrubland/ Detailed/ Prior to construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
7.13	6.5	Audit Pitcher Plant protection measures	Tuen Mun Area 46	Contractor	TMEIA		Y		✓
7.13	6.5	The loss of habitat shall be supplemented by enhancement planting in accordance with the landscape mitigation schedule.	All areas / As soon as accessible	Contractor	TMEIA		Y		✓
7.13	6.5	Spoil heaps shall be covered at all times.	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Avoid damage and disturbance to the remaining and surrounding natural habitat	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Placement of equipment in designated areas within the existing disturbed land	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Disturbed areas to be reinstated immediately after completion of the works.	All areas / Throughout construction period	Contractor	TMEIA		Y		✓
7.13	6.5	Construction activities should be restricted to the proposed works boundary	All areas / Throughout construction	Contractor	TMEIA		Y		✓

**Landfill Gas Hazard Assessment**

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	
14.12.2	14.2	<u>Appointment of Safety Officer</u> Appoint a properly trained safety officer and provide with appropriate equipment to measure and monitor LFG hazard. The monitoring frequency and areas to be monitored should be set down prior to commencement of ground-works either by the Safety Officer or an approved and appropriately qualified person.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures - Excavation</u>	Construction Stage	Contractor	EPD/TR8/97 -		Y		✓

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		Staff should receive appropriate training on working in areas susceptible to landfill gas, fire and explosion hazards. Excavation procedures and code of practice should be implemented.			Landfill Gas Hazard Assessment Guidance Note				
14.12.2	-	<u>Safety Measures – Welding, Flame- Cutting and Hot works</u> Hot works should be confined to open areas away from any trench or excavation. Should hot works must be carried out in trenches or confined space, “permit to work” procedures should be followed.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures – Enclosed Spaces</u> Site offices or buildings located within PPV Landfill Consultation Zone which have the capacity to accumulate landfill gas, then they should either be located in an area which has been proven to be free of landfill gas; or be raised clear of the ground by a minimum of 500mm.	Site office, building, tunnel, subway, confined area / Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures – Electrical Equipment</u> Any electrical equipment, such as motors and extension cords, should be intrinsically safe.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures – Piping</u> During piping assembly or conduiting construction, all valves/seals should be closed immediately after installation. As construction progresses, all valves/seals should be closed as installed to prevent the migration of gases through the pipeline/conduit. All piping/conduiting should be capped at the end of each working day.	Services & utilities / Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.2	-	<u>Safety Measures – Fire Safety</u> Adequate fire safety equipments should be provided on site. Workers and visitors should be notified of the potential fire hazards. Safety notices should be	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment		Y		✓

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		posted around the site warning the anger and potential hazards.			Guidance Note				
14.12.1	-	<u>Safety Measures – Confined Spaces</u> Precautionary measures should include ensuring that staff members are aware of the potential hazards of working in confined spaces, and that appropriate monitoring procedures are in place to prevent hazards in confined spaces.	Confined space / Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓
14.12.1	-	<u>Monitoring</u> Periodically during ground-works within the Consultation Zone, the works area should be monitored for methane, carbon dioxide and oxygen using appropriately calibrated portable gas detection equipment. Depending on the results of the measurements, actions required will vary. As a minimum these should encompass those actions specified in Table 14.8 of the EIA Report or Table 14.1 of the EM&A Manual.	Construction Stage	Contractor	EPD/TR8/97 - Landfill Gas Hazard Assessment Guidance Note		Y		✓

**Landscape and Visual**

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	
10.9	7.6	Existing trees on boundary of the Project Area shall be carefully protected during construction. Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. (Tree protection measures will be detailed at Tree Removal Application stage) (CM1)	All areas/detailed design/ during construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Trees unavoidably affected by the works shall be transplanted where practical. Trees will be	All areas/detailed design/ during	Design Consultant/	TMEIA	Y	Y		NA

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		transplanted straight to their final receptor site and not held in a temporary nursery. A detailed Tree Transplanting Specification shall be provided in the Contract Specification. Sufficient time for necessary tree root and crown preparation periods shall be allowed in the project programme (CM2)	construction	Contractor					
10.9	7.6	Hillside and roadside screen planting to proposed roads, associated structures and slope works (CM3)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y		NA
10.9	7.6	Hydroseeding or sheeting of soil stockpiles with visually unobtrusive material (in earth tone) (CM4)	All areas/detailed design/ during Construction/ post construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Screening of construction works by hoardings around works area in visually unobtrusive colours, to screen works (CM5)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		<>
10.9	7.6	Control night-time lighting and glare by hooding all lights (CM6)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Ensure no run-off into water body adjacent to the Project Area (CM7)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (CM8)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Recycle/Reuse all felled trees and vegetation, e.g. mulching (CM9)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		✓
10.9	7.6	Compensatory tree planting shall be provided to the satisfaction of relevant Government departments. Required numbers and locations of compensatory trees shall be determined and agreed separately with Government during the Tree Felling Application process under ETWBTC 3/2006 (CM10)	All areas/detailed design/ during Construction	Design Consultant/ Contractor	TMEIA	Y	Y		NA
10.9	7.6	Re-vegetation of affected woodland/shrubland with	All areas/detailed design/ during Construction	Design	TMEIA	Y	Y	Y	N/A



**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		native species (OM1)	during Construction/ construction	post	Consultant/ Contractor					
10.9	7.6	Tall buffer screen tree / shrub / climber planting where appropriate should be incorporated to soften hard engineering structures and facilities (OM2)	All areas/detailed design/ during Construction/ construction	post	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Streetscape elements (e.g. paving, signage, street furniture, lighting etc.) shall be sensitively designed in a manner that responds to the local context, and minimises potential negative landscape and visual impacts. Lighting units should be directional and minimize unnecessary light spill (OM3)	All areas/detailed design/ during Construction/ construction	post	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Structure, ornamental tree / shrub / climber planting should be provided along roadside amenity strips, central dividers and newly formed slopes to enhance the townscape quality and further greenery enhancement (OM4)	All areas/detailed design/ during Construction/ construction	post	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Aesthetically pleasing design (visually unobtrusive and non-reflective) as regard to the form, material and finishes shall be incorporated to all buildings, engineering structures and associated infrastructure facilities (OM5)	All areas/detailed design/ during Construction/ construction	post	Design Consultant/ Contractor	TMEIA	Y	Y	Y	N/A
10.9	7.6	Avoidance of excessive height and bulk of buildings and structures (OM6)	All areas/detailed design/ during Construction/ construction	post	Design Consultant/ Contractor	TMEIA	Y	Y	Y	✓

**Waste**

EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	
12.6		The Contractor shall identify a coordinator for the management of waste.	Contract mobilisation	Contractor	TMEIA		Y		✓
12.6		The Contractor shall prepare and implement a Waste Management Plan which specifies procedures such	Contract mobilisation	Contractor	TMEIA, Works Branch		Y		✓

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		as a ticketing system, to facilitate tracking of loads and to ensure that illegal disposal of wastes does not occur, and protocols for the maintenance of records of the quantities of wastes generated, recycled and disposed. A recording system for the amount of waste generated, recycled and disposed (locations) should be established.			Technical Circular No. 5/99 for the Trip-ticket System for Disposal of Construction and Demolition Material				
12.6		The Contractor shall apply for and obtain the appropriate licenses for the disposal of public fill, chemical waste and effluent discharges.	Contract mobilisation	Contractor	TMEIA, Land (Miscellaneous Provisions) Ordinance (Cap 28); Waste Disposal Ordinance (Cap 354); Dumping at Sea Ordinance (Cap 466); Water Pollution Control Ordinance.		Y		✓
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedures including waste reduction, reuse and recycling	Contract mobilisation	Contractor	TMEIA		Y		✓
12.6	8.1	The extent of cutting operation should be optimised where possible. Earth retaining structures and bored pile walls should be proposed to minimize the extent of cutting.	All areas / throughout construction period	Contractor	TMEIA		Y		✓

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

12.6	8.1	Inert C&D materials from the toll plaza cut slopes shall be reused for construction of the raised platform for the toll plaza where possible.	Toll Plaza / toll plaza construction period	Contractor	TMEIA		Y		✓
12.6	8.1	The site and surroundings shall be kept tidy and litter free.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	No waste shall be burnt on site.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	The Contractor shall be prohibited from disposing of C&D materials at any sensitive locations. The Contractor should propose the final disposal sites in the EMP and WMP for approval before implementation.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Stockpiled material shall be covered by tarpaulin and /or watered as appropriate to prevent windblown dust/ surface run off.	All areas / throughout construction period	Contractor	TMEIA		Y		◇
12.6	8.1	Excavated material in trucks shall be covered by tarpaulins to reduce the potential for spillage and dust generation.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Wheel washing facilities shall be used by all trucks leaving the site to prevent transfer of mud onto public roads.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Standard formwork or pre-fabrication should be used as far as practicable so as to minimise the C&D materials arising. The use of more durable formwork/ plastic facing for construction works should be considered. The use of wooden hoardings should be avoided and metal hoarding should be used to facilitate recycling. Purchasing of construction materials should avoid over-ordering and wastage.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	The Contractor should recycle as many C&D materials (this is a waste section) as possible on-site. The public fill and C&D waste should be segregated and stored in separate containers or skips to facilitate the reuse or recycling of materials and proper	All areas / throughout construction period	Contractor	TMEIA		Y		✓

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		disposal. Where practicable, the concrete and masonry should be crushed and used as fill materials. Steel reinforcement bar should be collected for use by scrap steel mills. Different areas of the sites should be considered for segregation and storage activities.							
12.6	8.1	All falsework will be steel instead of wood.	All areas / throughout construction period	Contractor	TMEIA		Y		◇
12.6	8.1	Chemical waste producers should register with the EPD. Chemical waste should be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows: <ul style="list-style-type: none"> <li>• suitable for the substance to be held, resistant to corrosion, maintained in good conditions and securely closed;</li> <li>• Having a capacity of &lt;450L unless the specifications have been approved by the EPD; and</li> <li>• Displaying a label in English and Chinese according to the instructions prescribed in Schedule 2 of the Regulations.</li> <li>• Clearly labelled and used solely for the storage of chemical wastes;</li> <li>• Enclosed with at least 3 sides;</li> <li>• Impermeable floor and bund with capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in the area, whichever is greatest;</li> <li>• Adequate ventilation;</li> <li>• Sufficiently covered to prevent rainfall entering (water collected within the bund must be tested and disposed of as chemical waste, if necessary); and</li> <li>• Incompatible materials are adequately separated.</li> </ul>	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Waste oils, chemicals or solvents shall not be	All areas / throughout	Contractor	TMEIA		Y		✓

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		disposed of to drain,	construction period						
12.6	8.1	Adequate numbers of portable toilets should be provided for on-site workers. Portable toilets should be maintained in reasonable states, which will not deter the workers from utilising them.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Night soil should be regularly collected by licensed collectors.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	General refuse arising on-site should be stored in enclosed bins or compaction units separately from C&D and chemical wastes. Sufficient dustbins shall be provided for storage of waste as required under the Public Cleansing and Prevention of Nuisances By-laws. In addition, general refuse shall be cleared daily and shall be disposed of to the nearest licensed landfill or refuse transfer station. Burning of refuse on construction sites is prohibited.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	All waste containers shall be in a secure area on hardstanding;	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Training shall be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including waste reduction, reuse and recycling.	All areas / throughout construction period	Contractor	TMEIA		Y		✓
12.6	8.1	Office wastes can be reduced by recycling of paper if such volume is sufficiently large to warrant collection. Participation in a local collection scheme by the Contractor should be advocated. Waste separation facilities for paper, aluminum cans, plastic bottles, etc should be provided on-site.	Site Offices/ throughout construction period	Contractor	TMEIA		Y		✓
12.6	Section 8	EM&A of waste handling, storage, transportation, disposal procedures and documentation through the site audit programme shall be undertaken.	All areas / throughout construction period	Contractor	EM&A Manual		Y		✓
<b>Water Quality</b>									
EIA reference	EM&A Manual reference	Environmental Protection Measures	Location/ Timing	Implementation Agent	Relevant Standard or Requirement	Implementation Stages			Status
						D	C	O	

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

Land Works									
6.10	-	Wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	-	Sewage effluent and discharges from onsite kitchen facilities shall be directed to Government sewer in accordance with the Requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Temporary access roads should be surfaced with crushed stone or gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	-	Rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	-	Measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Open stockpiles of construction materials (e.g. aggregates and sand) on site should be covered with tarpaulin or similar fabric during rainstorms.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇
6.10	5.8	Manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇

**CONTRACT NO. HY/2013/12**

**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS  
ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

		materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers.							
6.10	-	Discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	All vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for off site disposal.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	The Contractor shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		✓
6.10	-	Waste oil should be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance.	All areas/ throughout construction period	Contractor	TM-EIAO Waste Disposal Ordinance		Y		✓
6.10	-	All fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank.	All areas/ throughout construction period	Contractor	TM-EIAO		Y		◇

**CONTRACT NO. HY/2013/12**  
**TUEN MUN – CHECK LAP KOK LINK – NORTHERN CONNECTION TOLL PLAZA AND ASSOCIATED WORKS**  
**ENVIRONMENTAL MITIGATION AND ENHANCEMENT MEASURE IMPLEMENTATION SCHEDULE**

6.10	Section 5	All construction works shall be subject to routine audit to ensure implementation of all EIA recommendations and good working practice.	All areas/ throughout construction period	Contractor	EM&A Manual		Y		✓
------	-----------	---	---	------------	-------------	--	---	--	---

Remarks:

- ✓ Compliance of Mitigation Measures
- <> Compliance of Mitigation Measures but need improvement.
- × Non-compliance of Mitigation Measures
- ▲ Non-compliance of Mitigation Measures but rectified by Contractor
- △ Deficiency of Mitigation Measures but rectified by Contractor
- N/A Not Applicable in Reporting Period
- # Amended against condition 3.13 of EP-354/2009/C

Legend: D=Design, C=Construction, O=Operation

Note: Funding Agent for all mitigation measures will be the Highways Department of the Hong Kong SAR Government



## **Appendix N**

### **Cumulative Statistics on Exceedance and Complaint**

**Table N-1 Statistical Summary of Environmental Exceedance**

Reporting Period	Environmental Aspect / Parameter	Environmental Performance	Event Exceedance	
			Reporting Period	Cumulative since project commencement
November 2017	Air Quality – 1-hour TSP	Action Level	4	22
		Limit Level	1	2
	Air Quality – 24-hour TSP	Action Level	0	1
		Limit Level	0	0

**Table N-2 Statistical Summary of Environmental Complaints**

Reporting Period	Environmental Complaint Statistics					
	Frequency	Cumulative	Complaint Nature			
			Air	Noise	Water	Others
November 2017	0	9	2	NA	6	1
Cumulative since project commencement	9	9	2	NA	6	1

**Table N-3 Statistical Summary of Environmental Summons**

Reporting Period	Environmental Summons Statistics				
	Frequency	Cumulative	Complaint Nature		
			Air	Noise	Water
November 2017	0	0	NA	NA	NA
Cumulative since project commencement	0	0	NA	NA	NA

**Table N-4 Statistical Summary of Environmental Prosecution**

Reporting Period	Environmental Prosecution Statistics				
	Frequency	Cumulative	Complaint Nature		
			Air	Noise	Water
November 2017	0	0	NA	NA	NA
Cumulative since project commencement	0	0	NA	NA	NA

**Appendix O**

**Investigation Report for the Complaint**

**Contract No. HY/2013/12**  
**Tuen Mun - Chek Lap Kok Link - Northern Connection Toll Plaza and Associated Works**

**Investigation Report on Action or Limit Level Non-compliance**

<b>Complaint Log No.</b>	TCS00715/14/300/F0343
<b>Received Date by ET</b>	25 October 2017
<b>Complaint Details</b>	<p>The District Councillor represents the resident who living at Tuen Mun Ferry Pier area to complain that light nuisance created by Tuen Mun - Chek Lap Kok Link Project during mid-night to cause serious impact for their rest.</p> <p>Also, the complaint query the schedule for the construction works and the mitigation measures to avoid light nuisance affect to the resident.</p>
<b>Complaint Location</b>	Tuen Mun - Chek Lap Kok Link Project
<b>Date of Complaint</b>	24 October 2017
<b>Environmental Aspect</b>	Light Nuisance
<b>Complainant</b>	District Councillor Mr. YAN Siu-nam
<b>Complaint Route</b>	via EPD
<b>Investigation Result</b>	<ol style="list-style-type: none"> <li>1 A complaint was received via EPD on 24 October 2017, regarding light nuisance created by Tuen Mun - Chek Lap Kok Link Project during night time.</li> <li>2 According to site record, only TTA maintenance works (cleaning water filled barrier, cleaning lanterns and fixing reflective stripes) and formtraveller works (Finishing works, concreting and Launch) was conducted at construction site for Project HY/2013/12 on night-time and the frequency is about 1 time per 1 to 2 weeks.</li> <li>3 Spotlight was used in the TTA works under the decking of TD1 for safety reason and all spotlights were pointing to the site area. (Ref. to Location Plan and Photo of TTA) For other works area only limited lighting was used. Also the contractor was properly implemented the landscape and visual mitigation measure under EMIS requirement to Control night-time lighting and glare by hooding all lights.</li> <li>4 Review the photo attached in the complaint letter and the join site inspection with ET, Contractor, ER and IEC on 7 November 2017, the light source is not located in the project HY/2013/12. (Ref. to location plan and photo taken in the join site inspection) Therefore we considered that the cause of complaint is not project related.</li> <li>5 Based on above investigation, the complaint is unlikely related to the Contract work and no corrective action was required accordingly. However, the Contractor is reminded that implemented L&amp;V mitigation measures during the construction period.</li> </ol>
<b>Action to be taken</b>	Nil

**Prepared By :** T.W. Tam

**Designation :** Environmental Team Leader

**Signature :** 

**Date :** 27 November 2017

**Location Plan:**

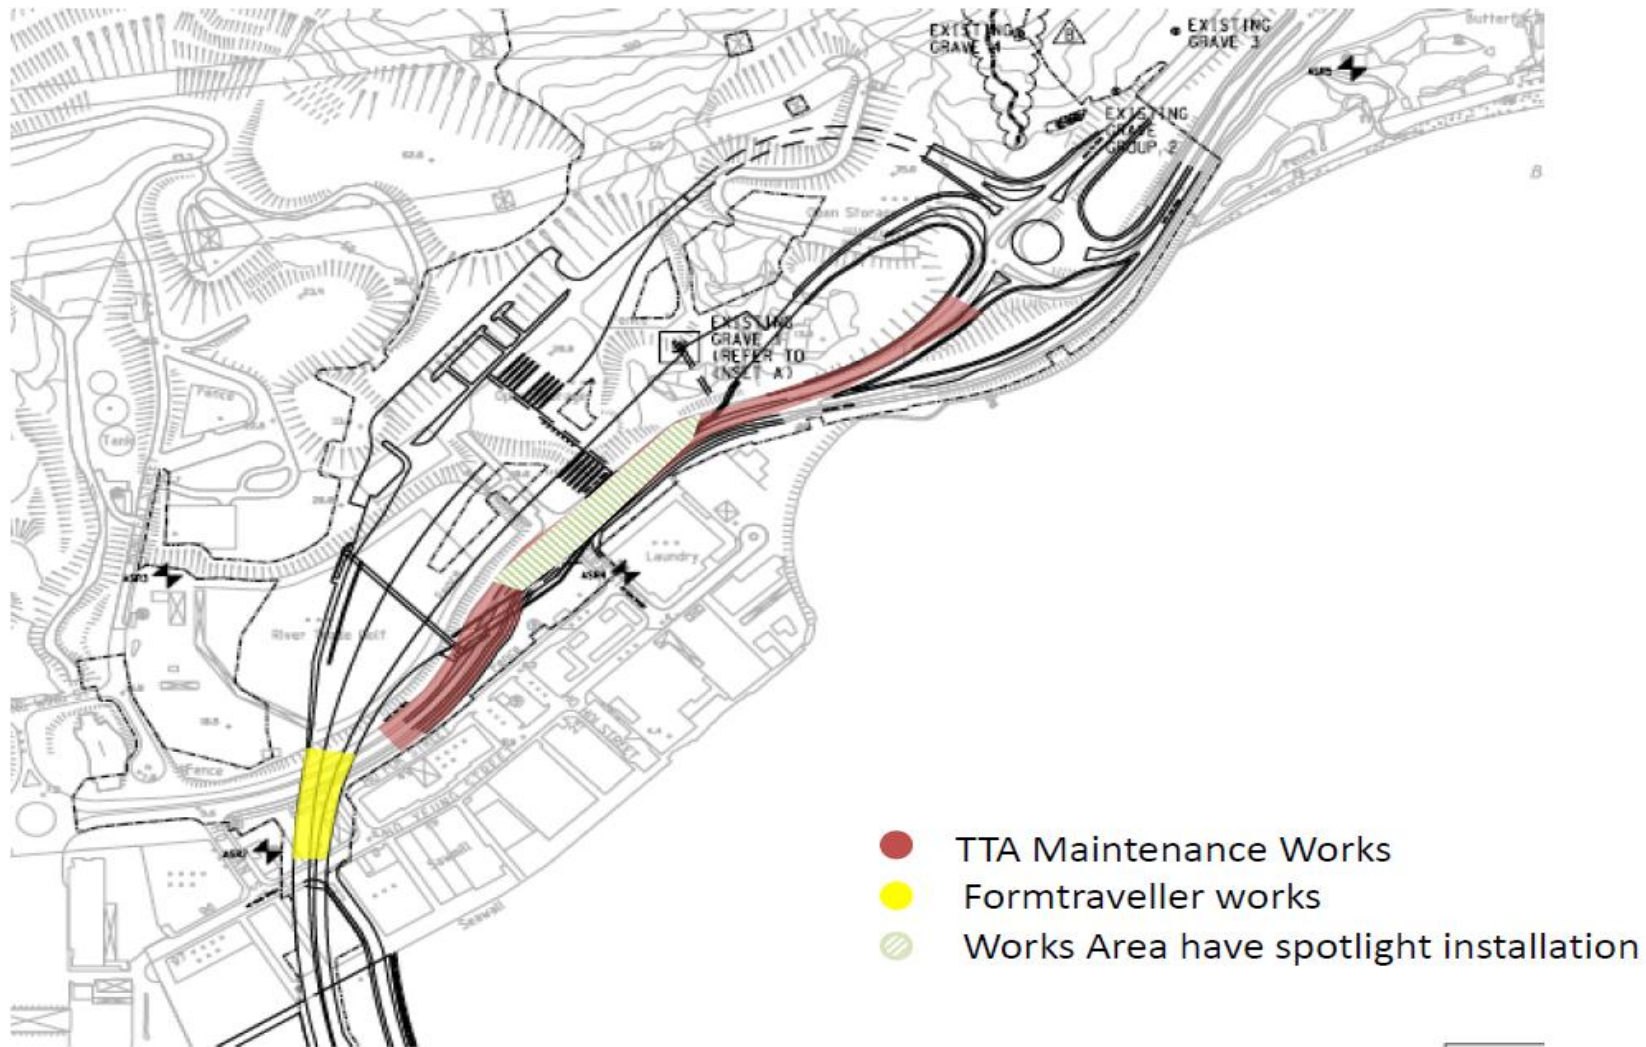




Photo of Light Nuisance in the Complaint Letter





Photo of Join Site Inspection at Tune Mun Riviera Gardens




Photo Record



TTA works at Lung Mun Road during Night Time



Finishing works at formtraveller during Night Time and limited light was used




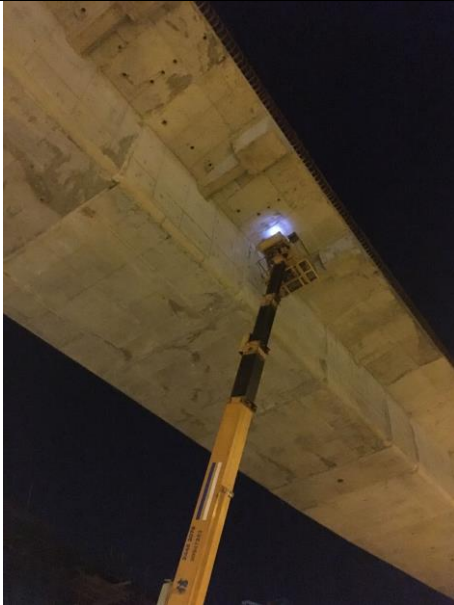


Limited lighting was used during night time





Finishing works at formtraveller during Night Time and limited light was used





**Photo Record for TTA works from August to early October**

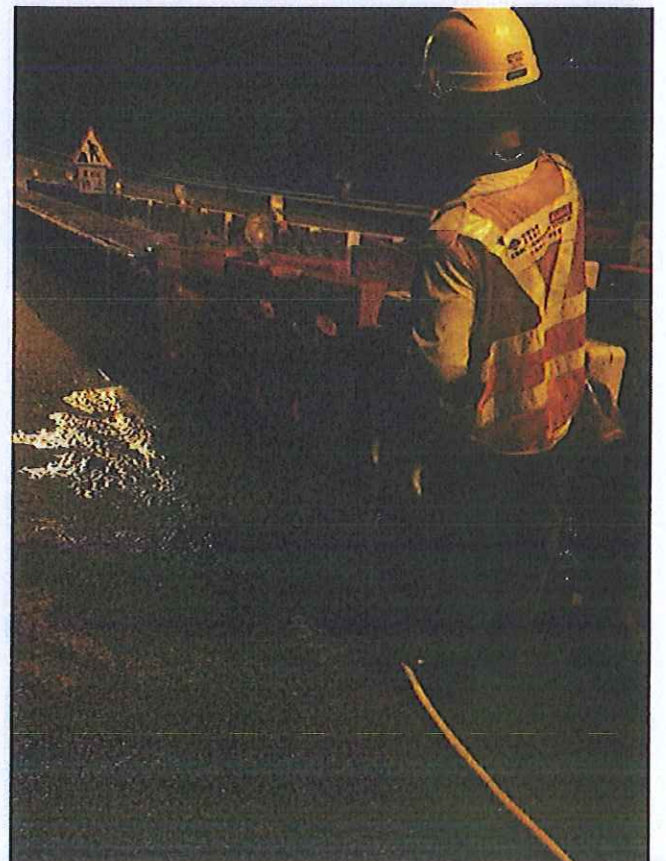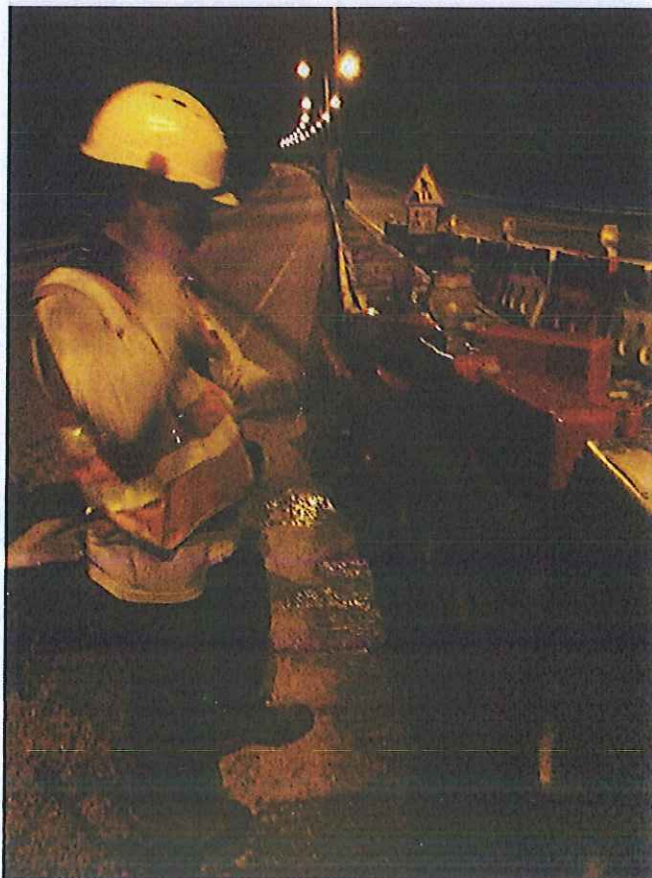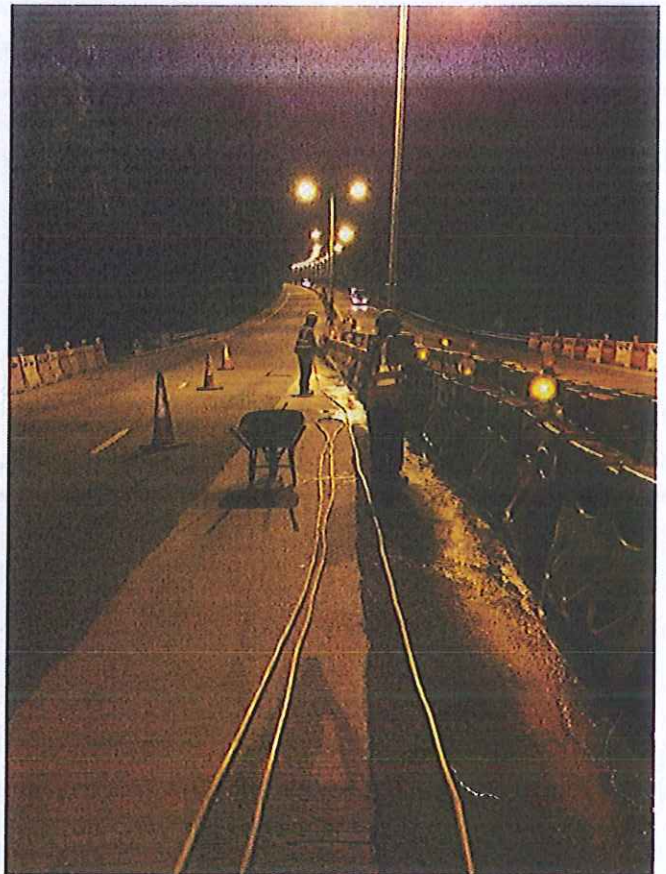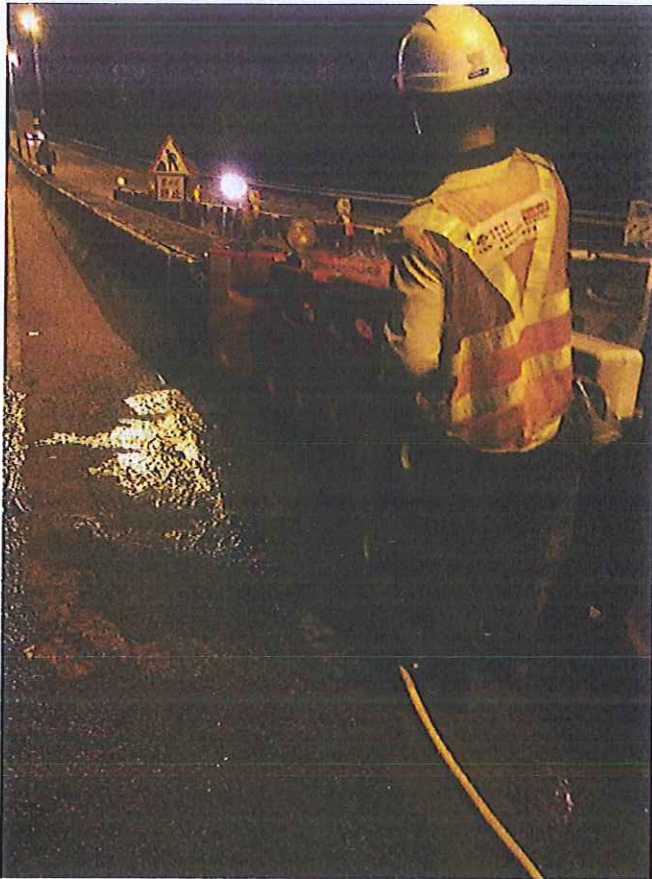





11 OCT 2017

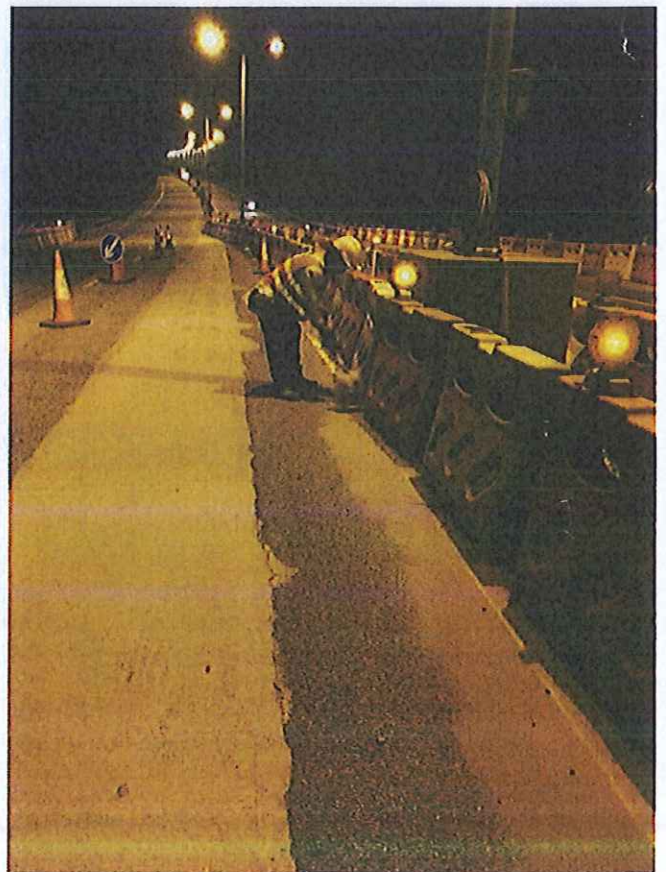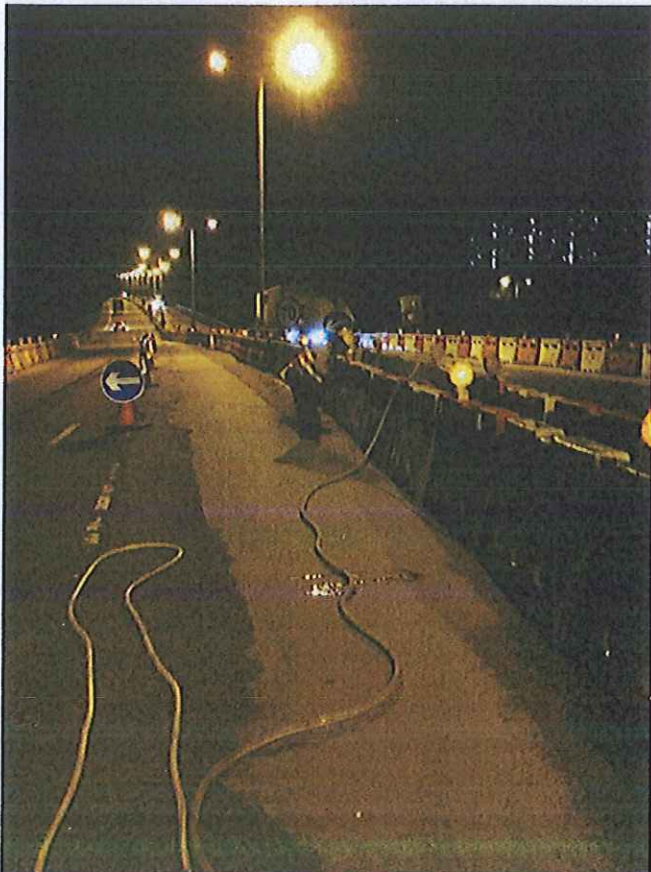





11 OCT 2017

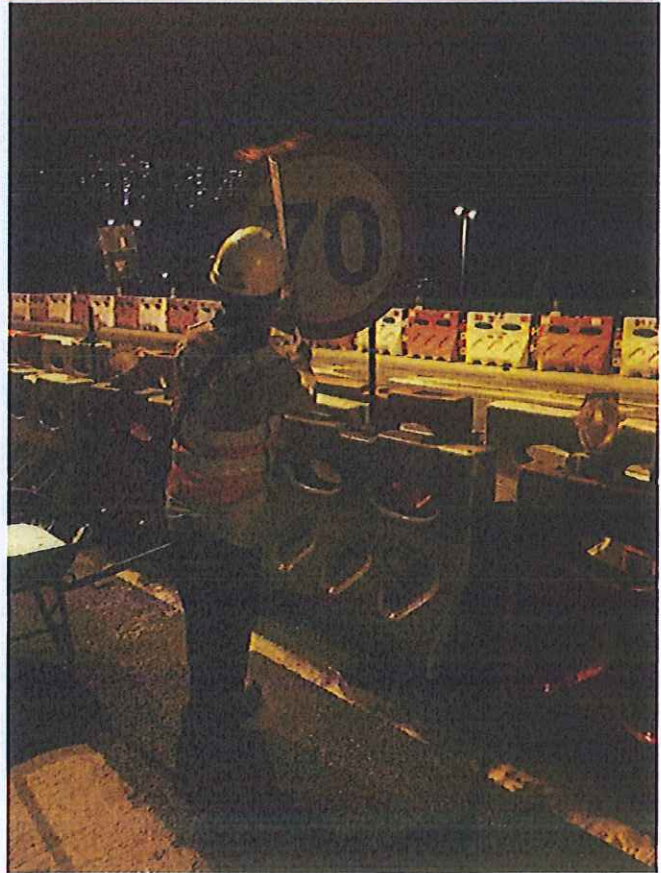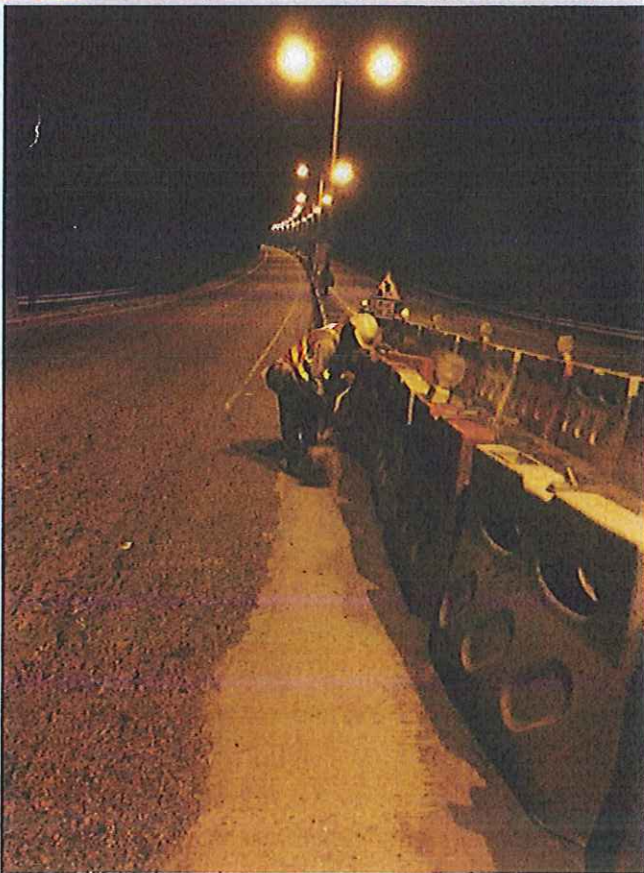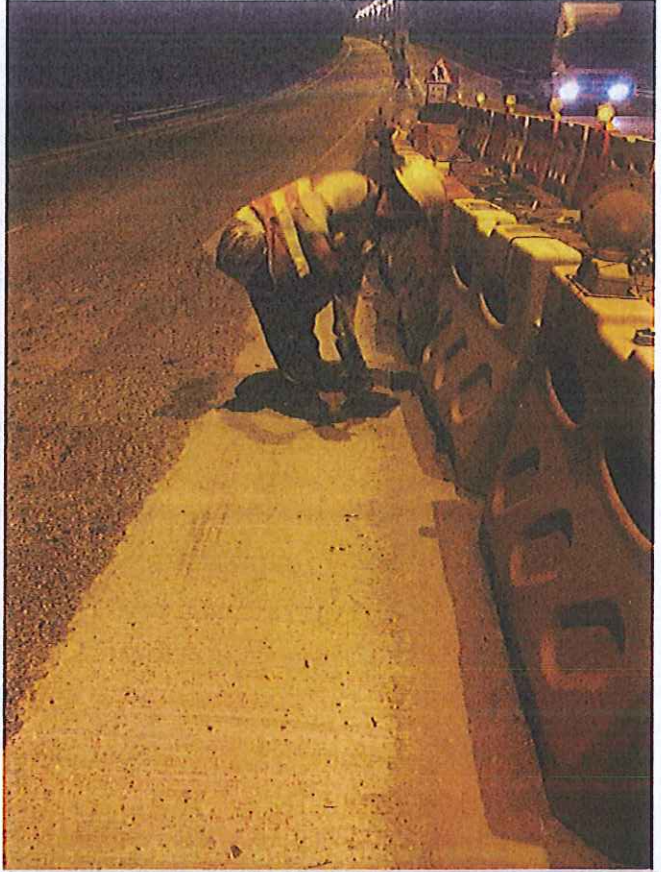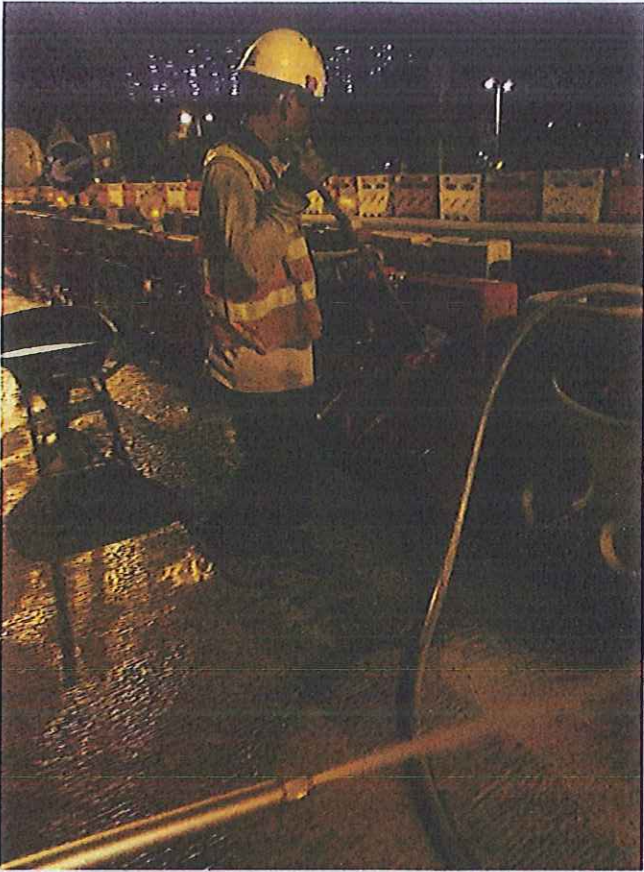

11 OCT 2017

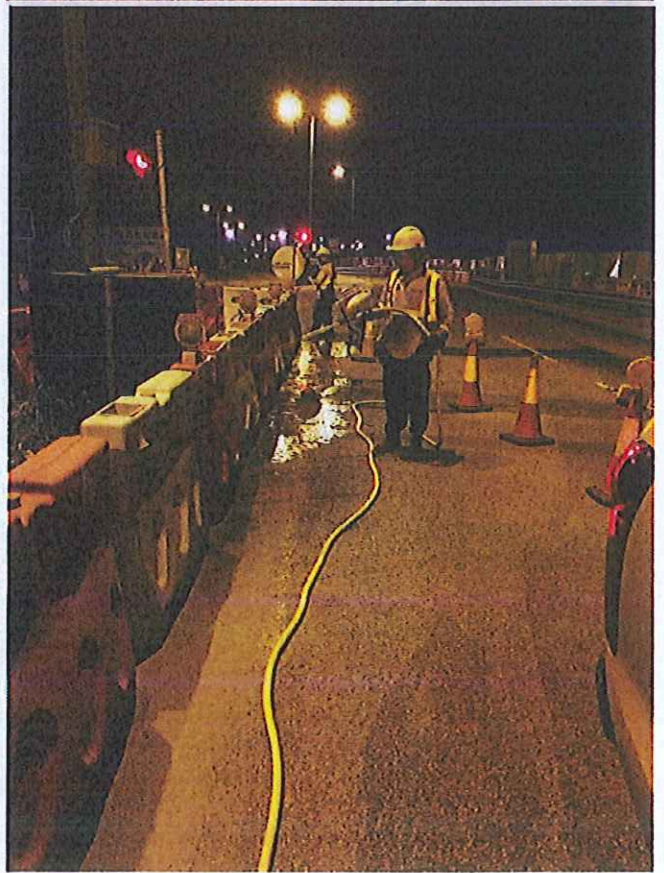
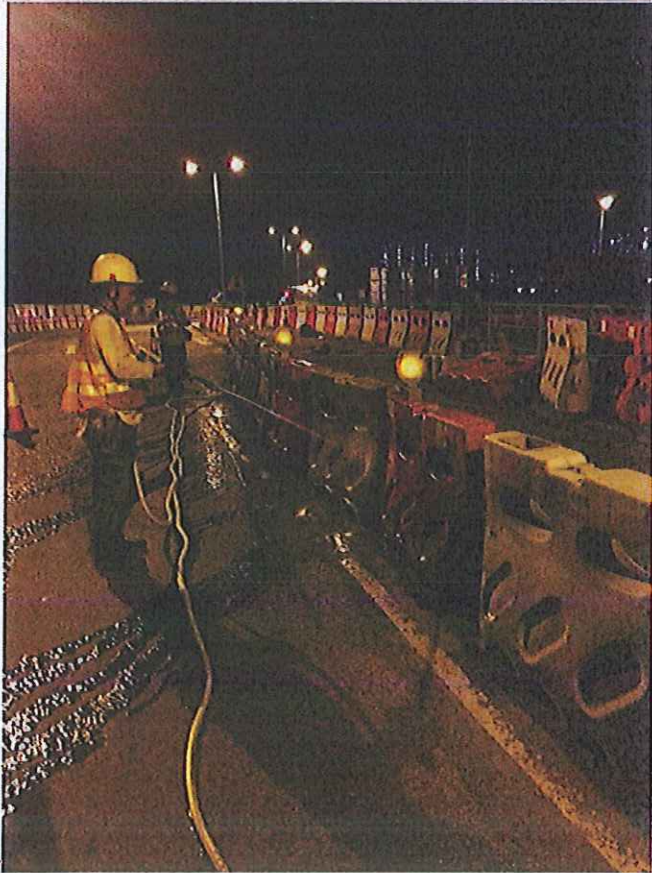
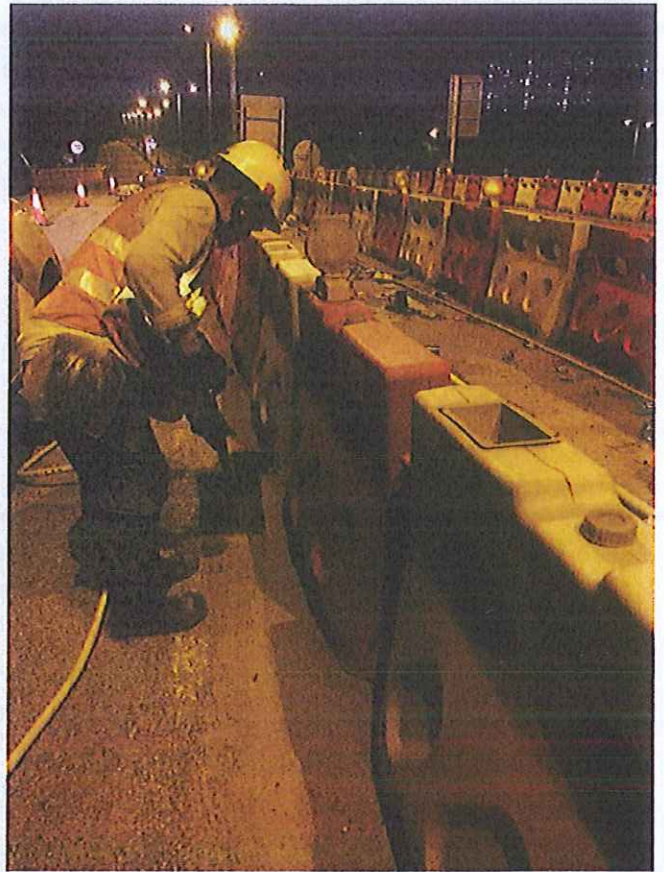
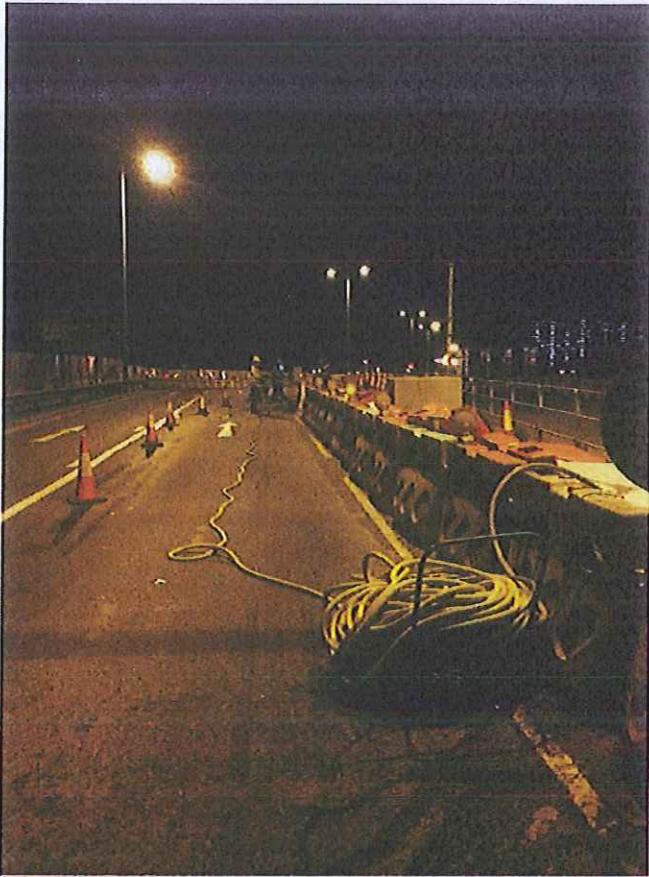


11 OCT 2017

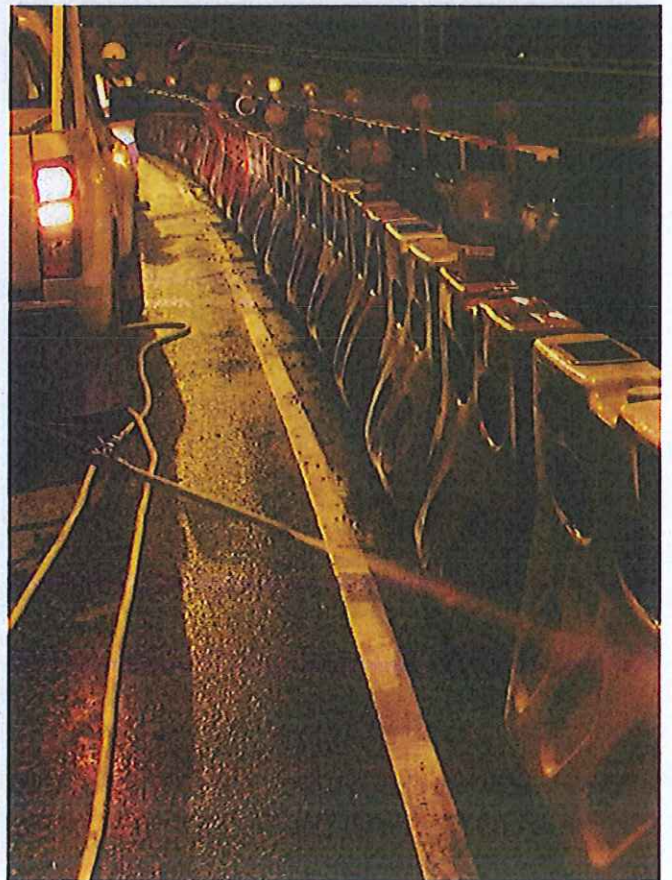
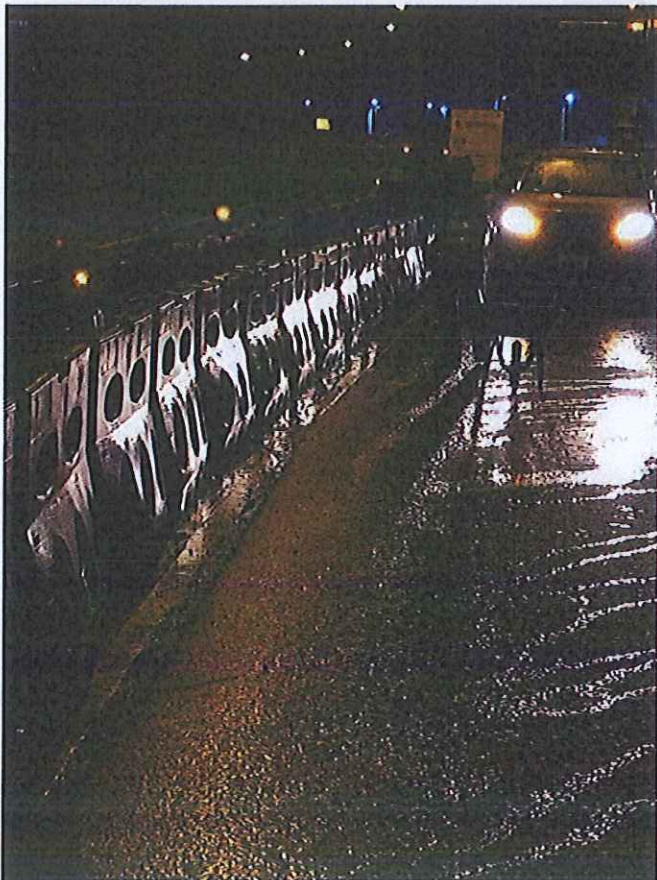
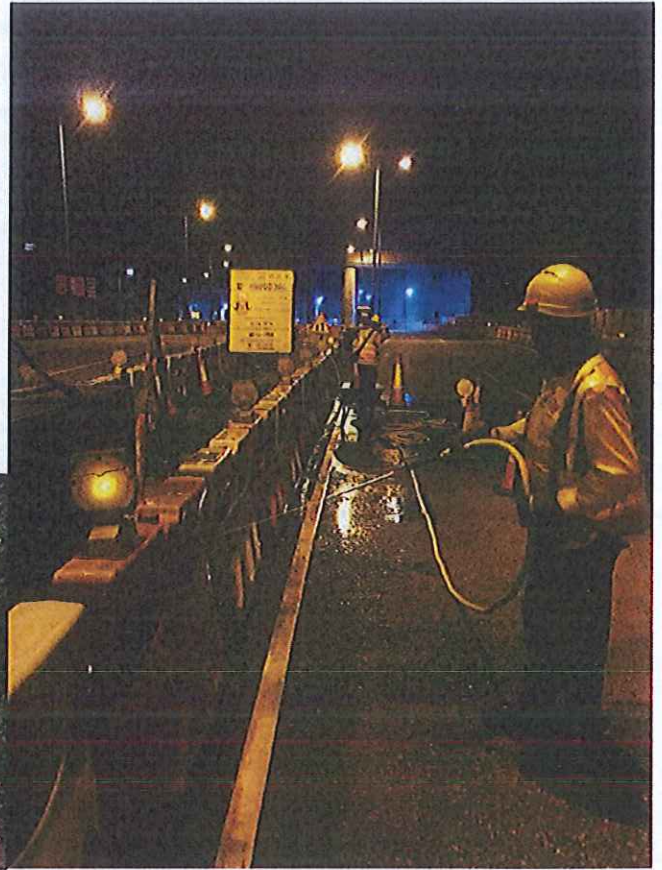
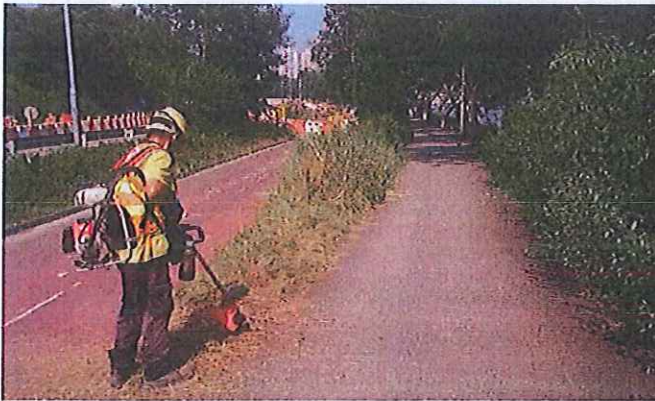


11 OCT 2017







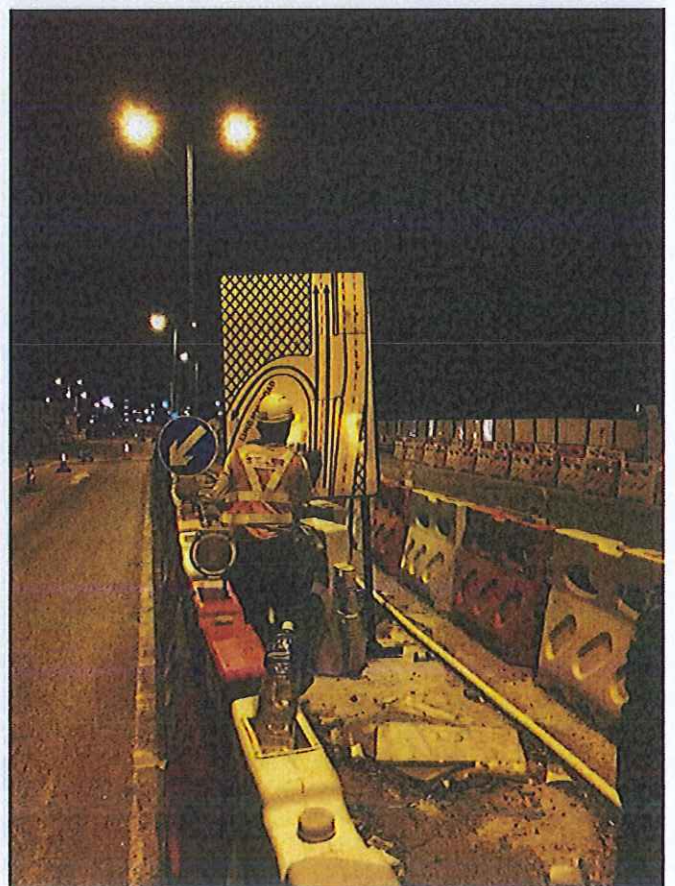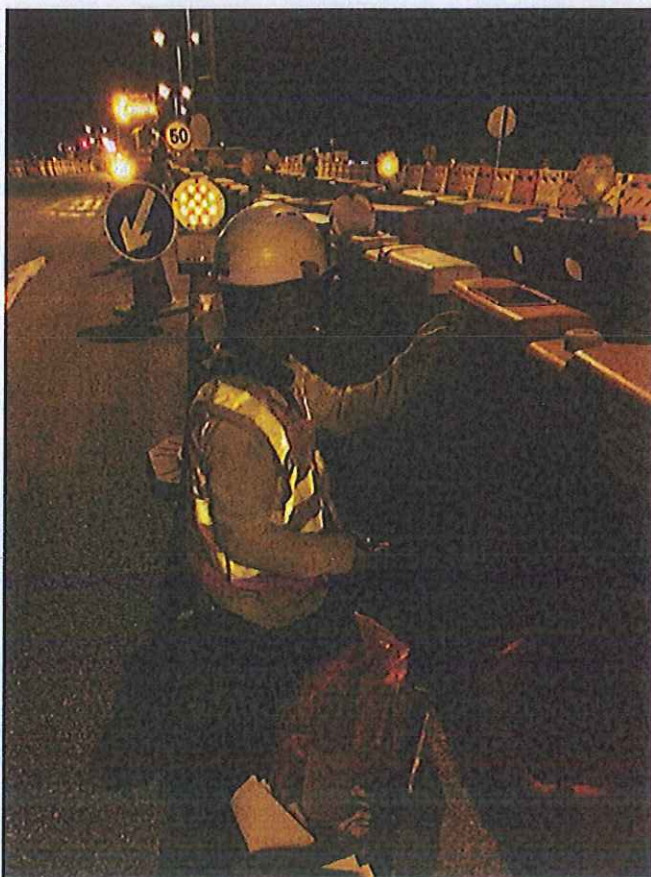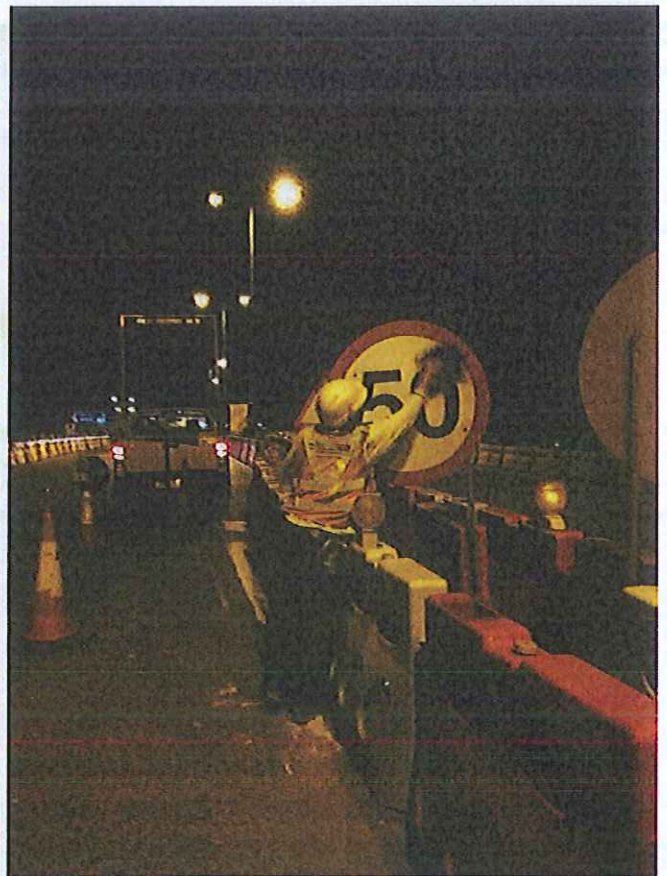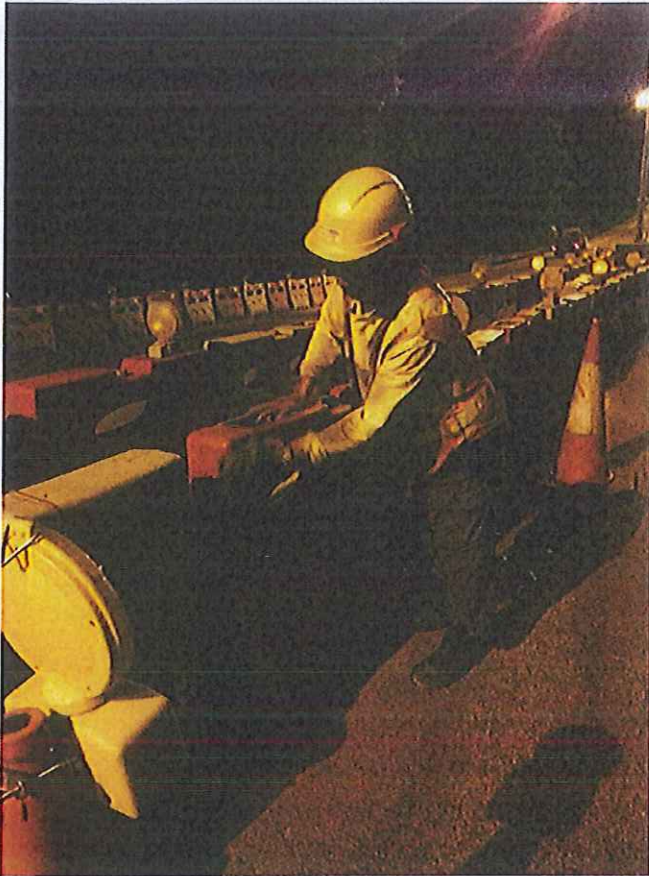





09 OCT 2017

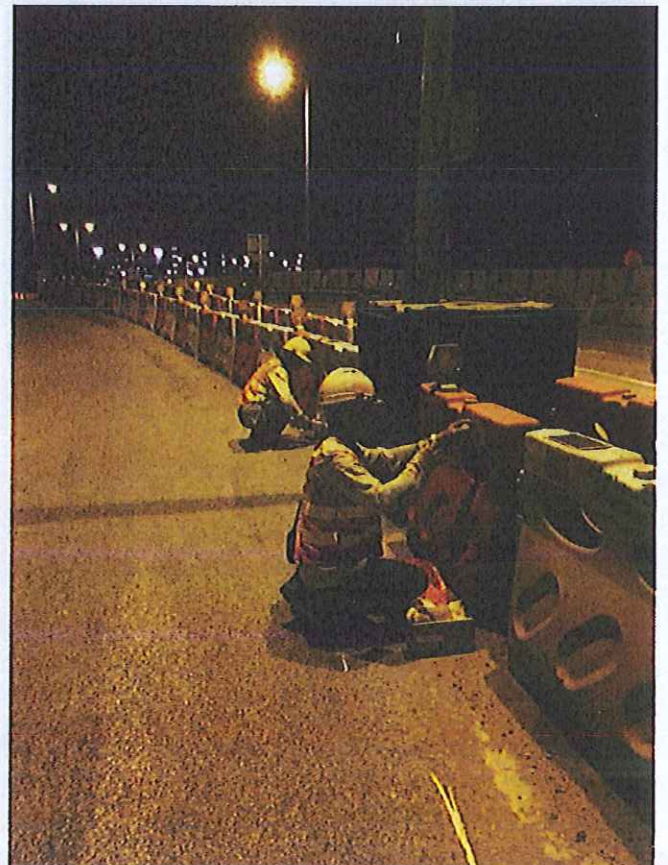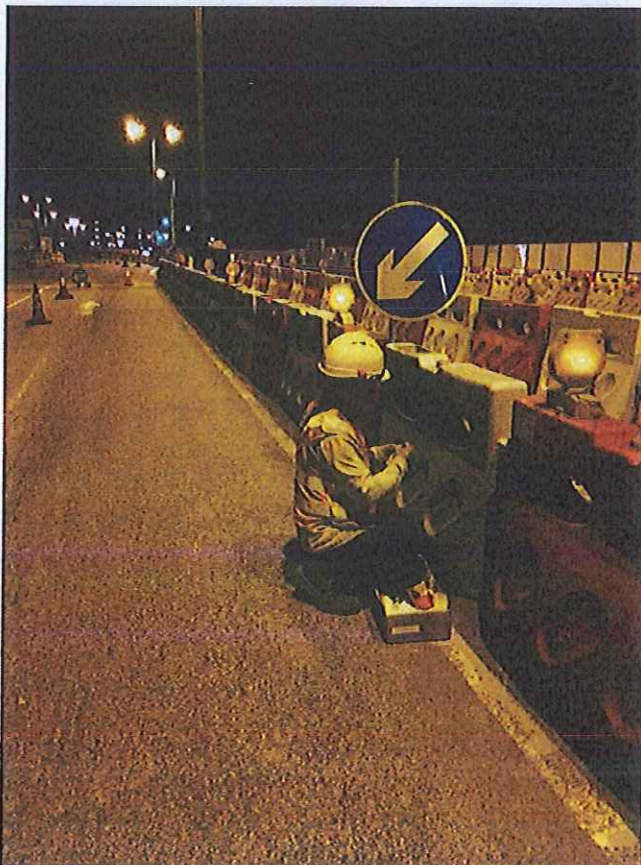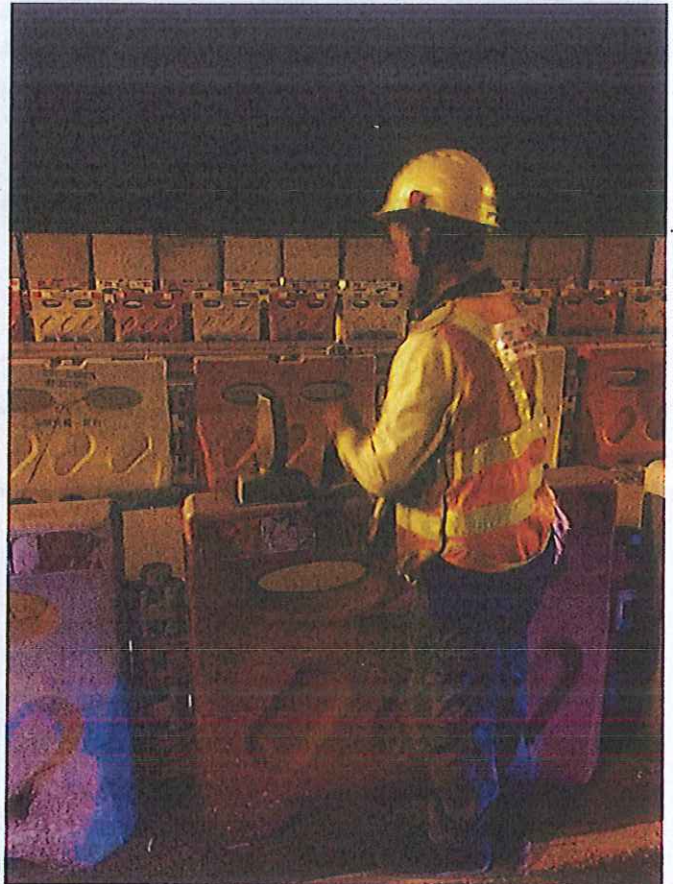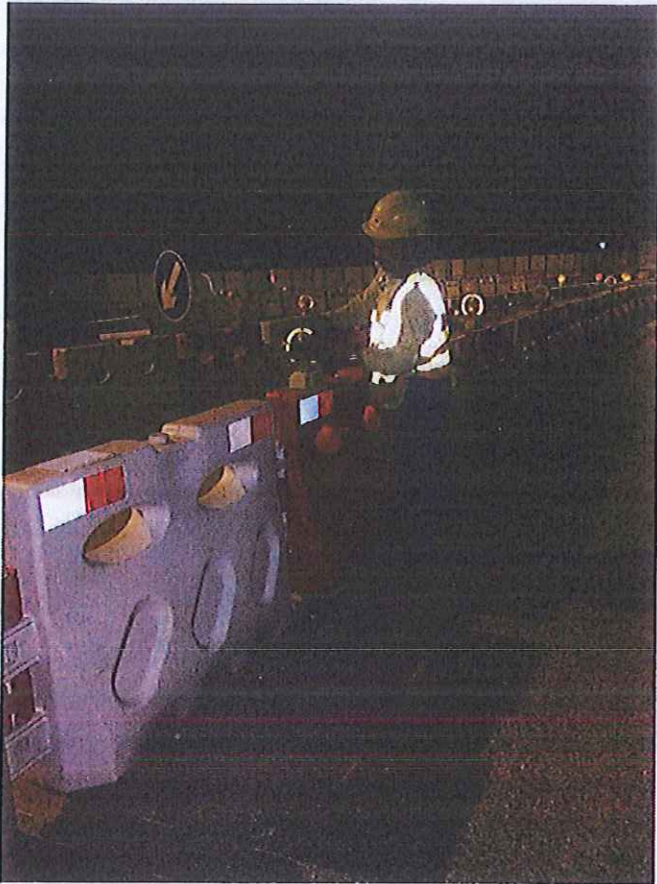




09 OCT 2017

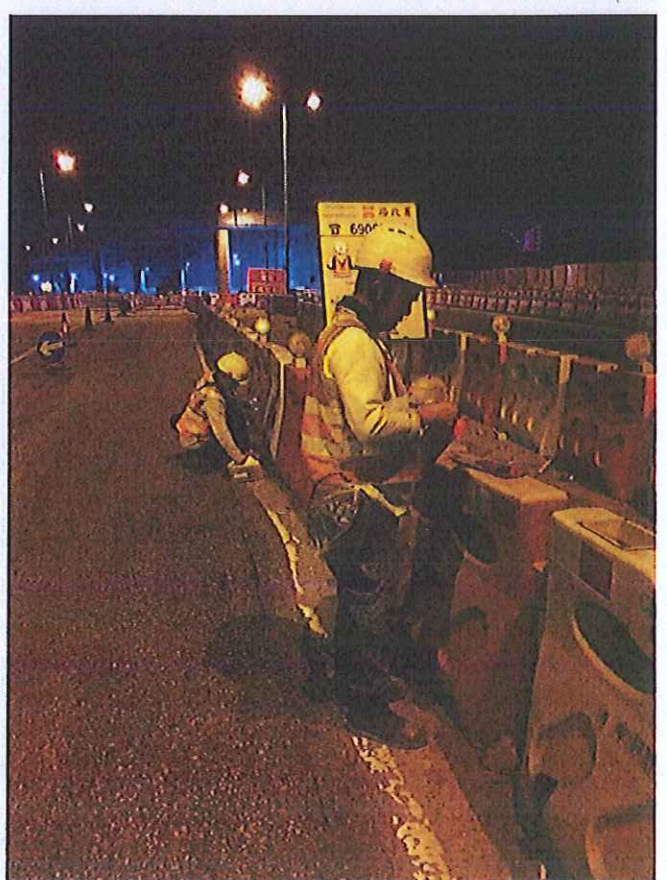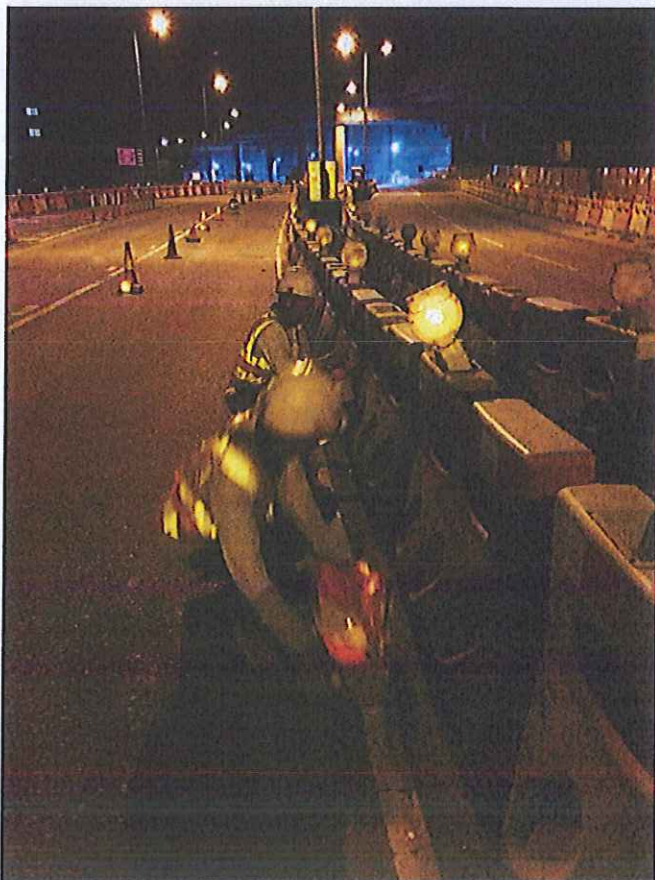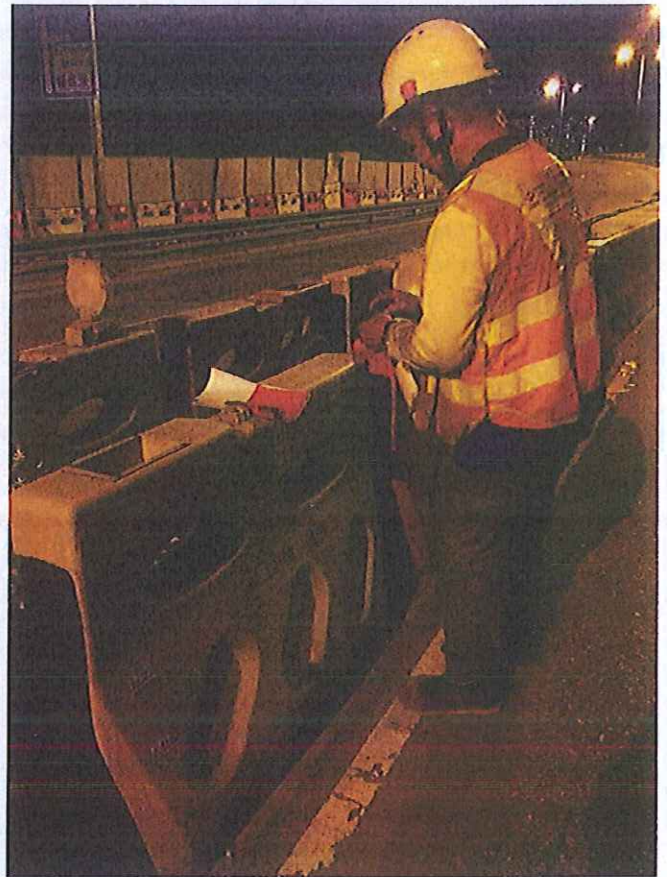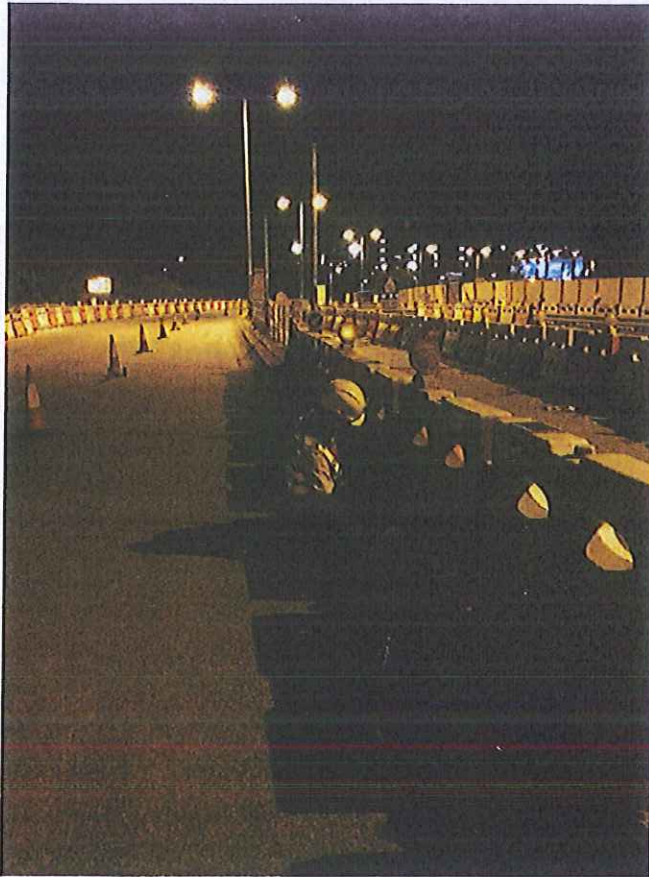



09 OCT 2017

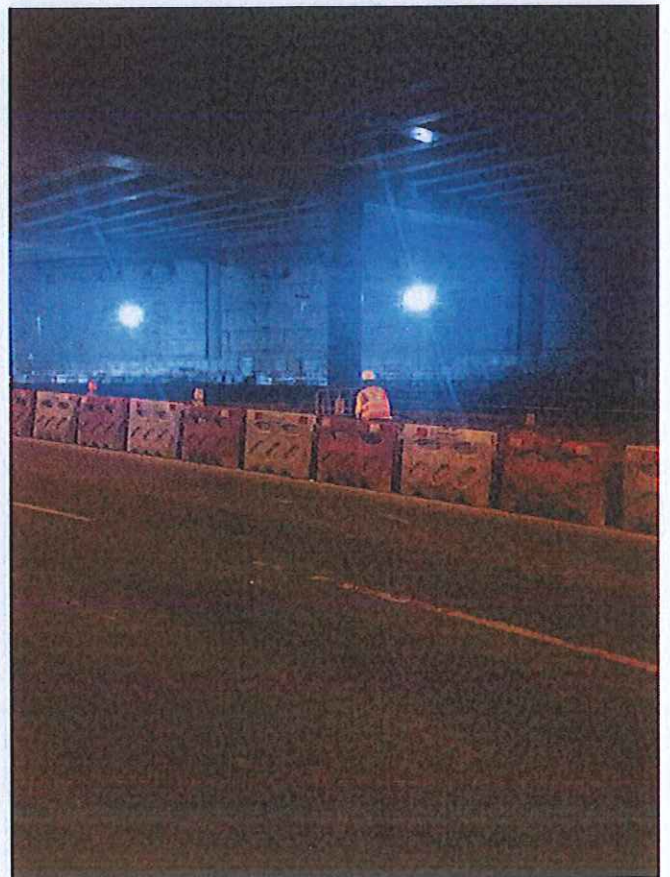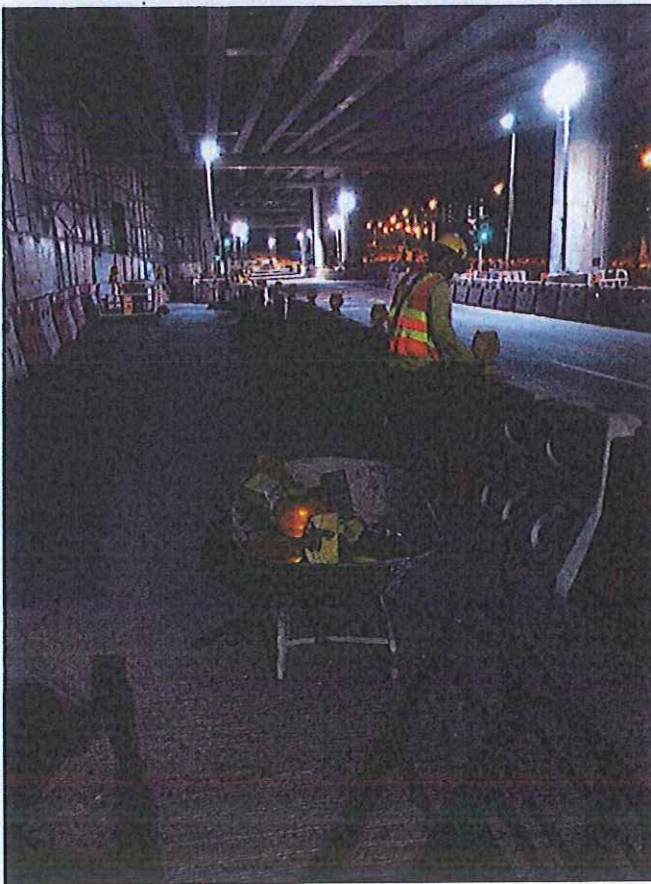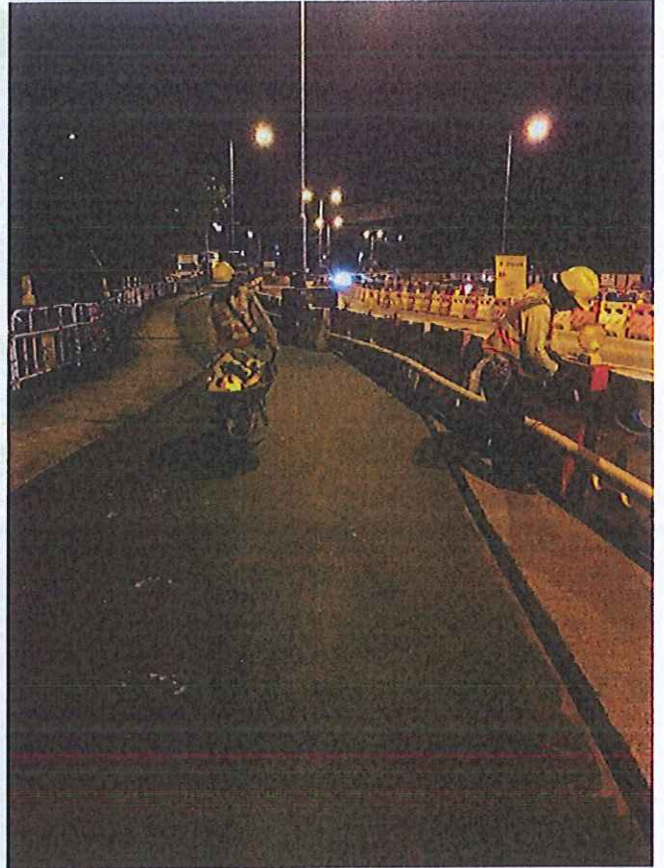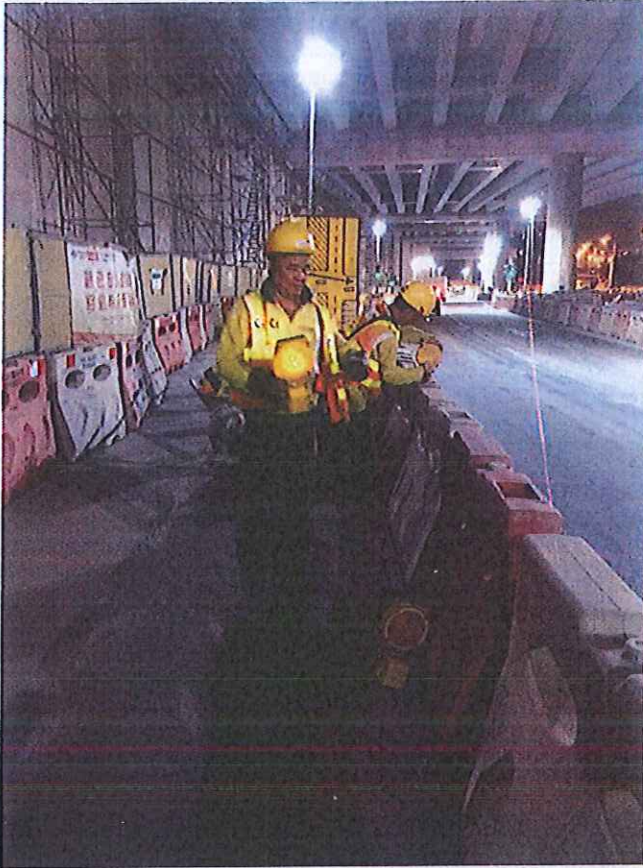

07 AUG 2017

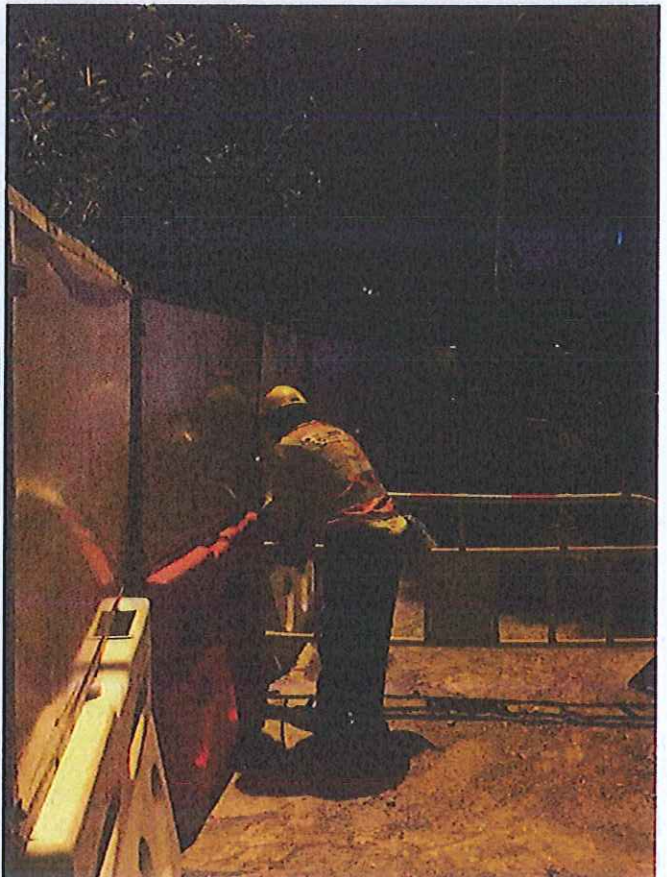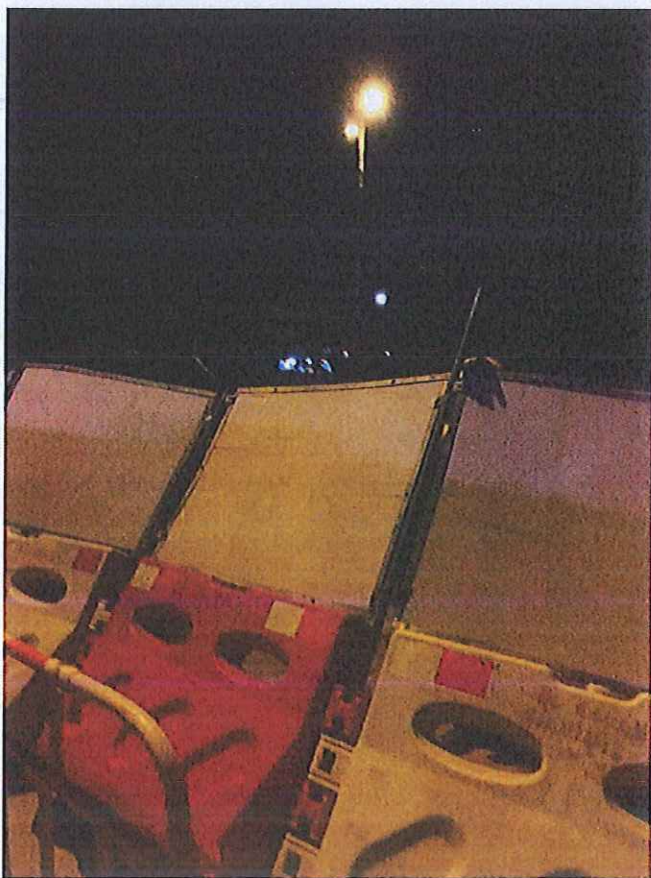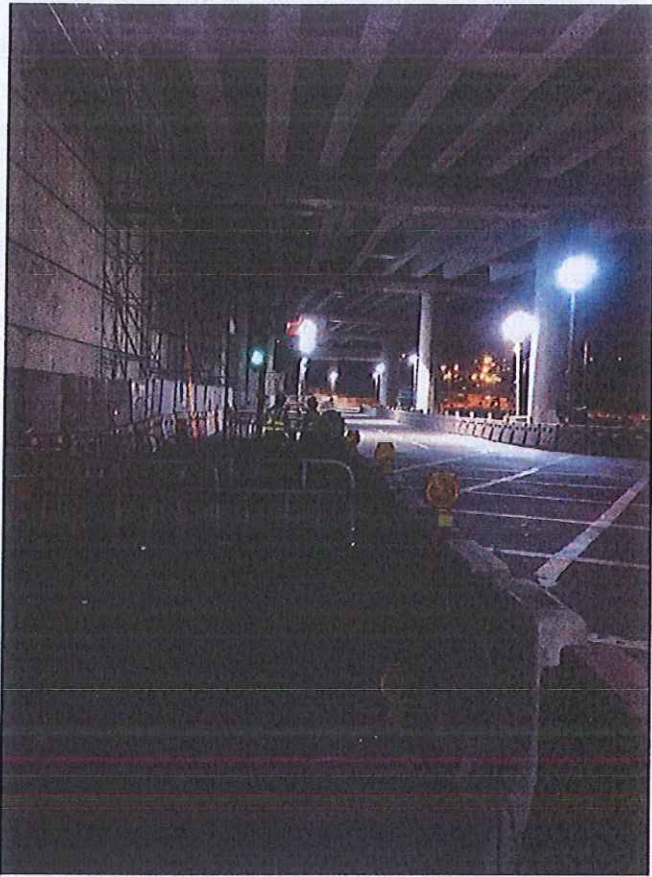

07 AUG 2017

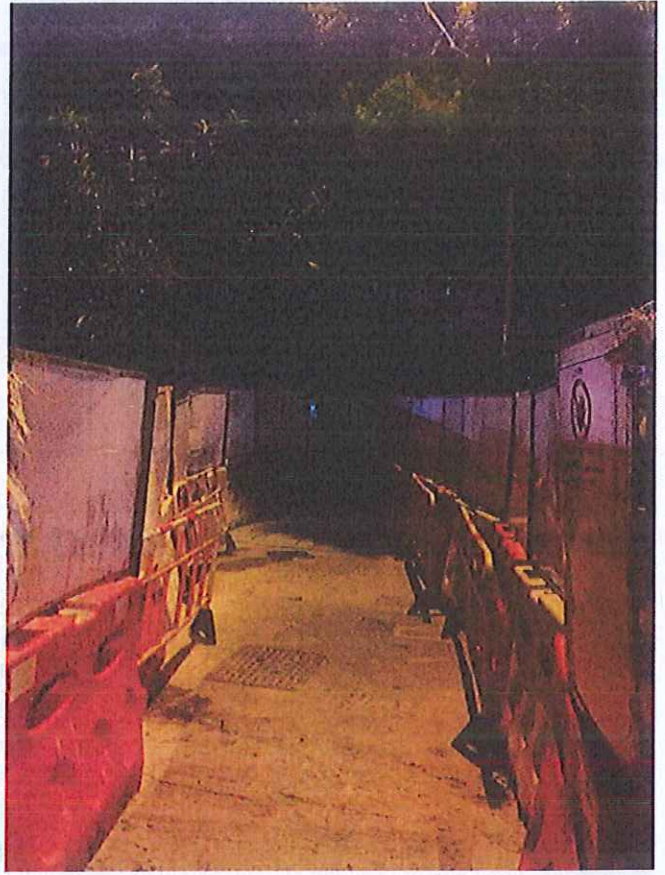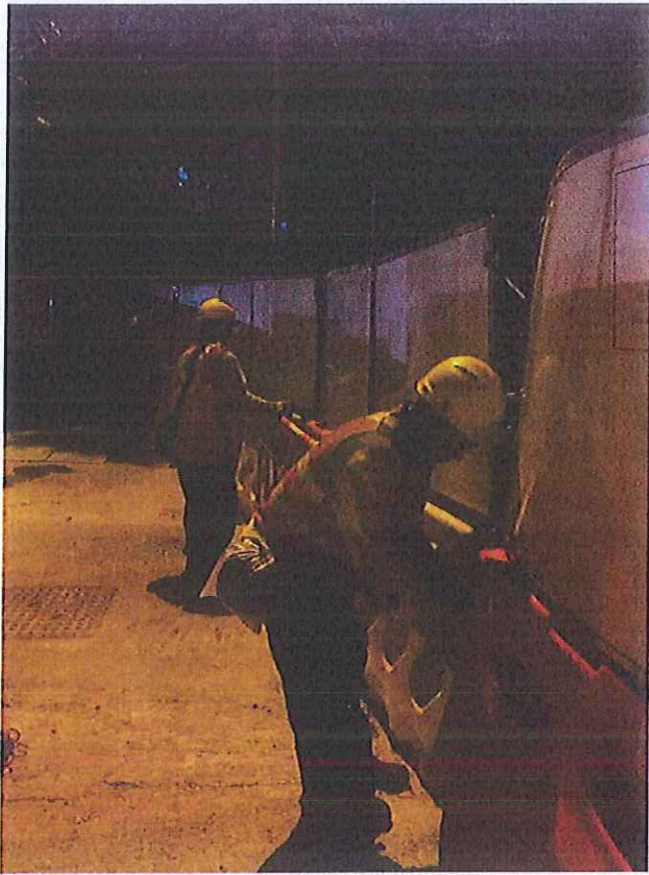

07 AUG 2017

**Appendix P**

**Inspection Checklist for  
Vulnerable to Contaminated Water Discharge**



Contract No. HY/2013/12  
 Tuen Mun - Chek Lap Kok Link Northern Connection Toll Plaza  
 and Associated Works

Inspection Checklist for vulnerable to contaminated water discharge

Inspection Date: 2017-11-01 Location: Stream B, Outfall 1  
 Name of Inspector: Tommy Law Position of Inspector: EO

Please put a tick  on the appropriate box.

Item Description		Y	P	N	Remarks
1	Exposed slope protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2	Adequacy of wastewater treatment facilities provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3	Sandbags provided at each step and top of side walls?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4	Is silt screen maintained in good condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5	Remove debris, grit and silt inside the drainage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
6	Contaminated water discharge at discharge point / drainage inlet avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
7	General housekeeping / site tidiness in good condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Legends: Y = Yes, P = Partial, N = No




## Daily Drainage Inspection Record

Inspection Date: 2017-11-01



Stream B Outfall: No water is discharging.

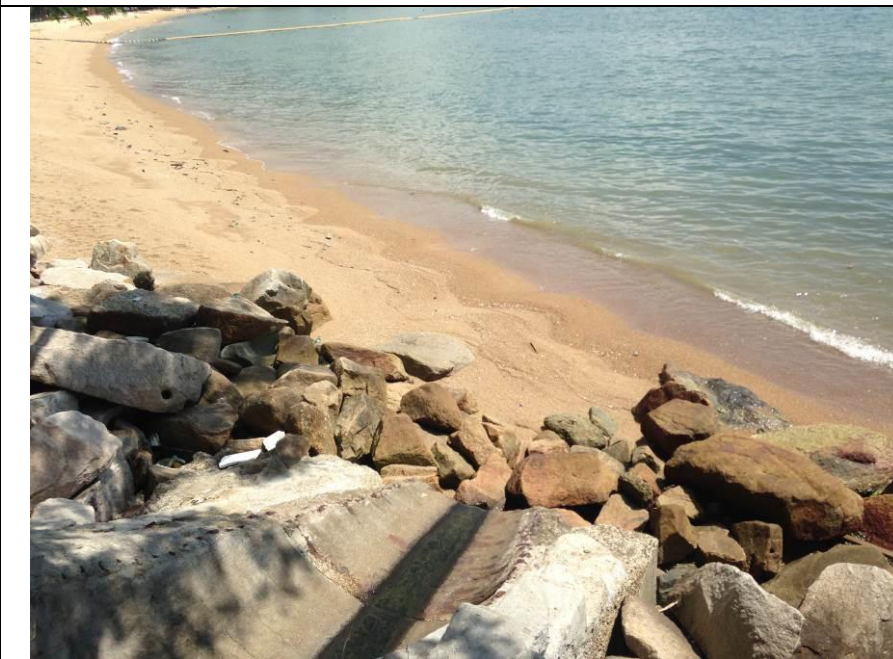

Outfall 1: No water is discharging.

Inspection Checklist for vulnerable to contaminated water discharge

Inspection Date: 2017-11-08                      Location: Stream B, Outfall 1  
 Name of Inspector: Tommy Law                      Position of Inspector: EO

Please put a tick  $\checkmark$  on the appropriate box.

Item Description		Y	P	N	Remarks
1	Exposed slope protected?	$\checkmark$			
2	Adequacy of wastewater treatment facilities provided?	$\checkmark$			
3	Sandbags provided at each step and top of side walls?	$\checkmark$			
4	Is silt screen maintained in good condition?	$\checkmark$			
5	Remove debris, grit and silt inside the drainage system?	$\checkmark$			
6	Contaminated water discharge at discharge point / drainage inlet avoided?	$\checkmark$			
7	General housekeeping / site tidiness in good condition?	$\checkmark$			

Legends: Y = Yes, P = Partial, N = No

## Daily Drainage Inspection Record

Inspection Date: 2017-11-08



Stream B Outfall: No water is discharging.



Outfall 1: No water is discharging.

Inspection Checklist for vulnerable to contaminated water discharge

Inspection Date: 2017-11-15 Location: Stream B, Outfall 1  
Name of Inspector: Tommy Law Position of Inspector: EO

Please put a tick  $\checkmark$  on the appropriate box.

Item Description		Y	P	N	Remarks
1	Exposed slope protected?	$\checkmark$			
2	Adequacy of wastewater treatment facilities provided?	$\checkmark$			
3	Sandbags provided at each step and top of side walls?	$\checkmark$			
4	Is silt screen maintained in good condition?	$\checkmark$			
5	Remove debris, grit and silt inside the drainage system?	$\checkmark$			
6	Contaminated water discharge at discharge point / drainage inlet avoided?	$\checkmark$			
7	General housekeeping / site tidiness in good condition?	$\checkmark$			

Legends: Y = Yes, P = Partial, N = No

## Daily Drainage Inspection Record

Inspection Date: 2017-11-15



Stream B Outfall: No water is discharging.



Outfall 1: No water is discharging.

Inspection Checklist for vulnerable to contaminated water discharge

Inspection Date: 2017-11-22 Location: Stream B, Outfall 1  
Name of Inspector: Tommy Law Position of Inspector: EO

Please put a tick  $\checkmark$  on the appropriate box.

Item Description		Y	P	N	Remarks
1	Exposed slope protected?	$\checkmark$			
2	Adequacy of wastewater treatment facilities provided?	$\checkmark$			
3	Sandbags provided at each step and top of side walls?	$\checkmark$			
4	Is silt screen maintained in good condition?	$\checkmark$			
5	Remove debris, grit and silt inside the drainage system?	$\checkmark$			
6	Contaminated water discharge at discharge point / drainage inlet avoided?	$\checkmark$			
7	General housekeeping / site tidiness in good condition?	$\checkmark$			

Legends: Y = Yes, P = Partial, N = No

## Daily Drainage Inspection Record

Inspection Date: 2017-11-22



Stream B Outfall: No water is discharging.



Outfall 1: No water is discharging.

Inspection Checklist for vulnerable to contaminated water discharge

Inspection Date: 2017-11-29 Location: Stream B, Outfall 1  
Name of Inspector: Tommy Law Position of Inspector: EO

Please put a tick  $\checkmark$  on the appropriate box.

Item Description		Y	P	N	Remarks
1	Exposed slope protected?	$\checkmark$			
2	Adequacy of wastewater treatment facilities provided?	$\checkmark$			
3	Sandbags provided at each step and top of side walls?	$\checkmark$			
4	Is silt screen maintained in good condition?	$\checkmark$			
5	Remove debris, grit and silt inside the drainage system?	$\checkmark$			
6	Contaminated water discharge at discharge point / drainage inlet avoided?	$\checkmark$			
7	General housekeeping / site tidiness in good condition?	$\checkmark$			

Legends: Y = Yes, P = Partial, N = No



## Daily Drainage Inspection Record

Inspection Date: 2017-11-29



Stream B Outfall: No water is discharging.



Outfall 1: No water is discharging.
