



CONTRACT NO: HK/2011/07

WANCHAI DEVELOPMENT PHASE II AND CENTRAL  
WANCHAI BYPASS  
SAMPLING, FIELD MEASUREMENT AND TESTING WORKS  
(STAGE 2)

ENVIRONMENTAL PERMIT NO. EP-356/2009,  
FURTHER ENVIRONMENTAL PERMIT NOS. FEP-02/356/2009,  
FEP-03/356/2009, FEP-04/356/2009 , FEP-06/356/2009 AND  
FEP-07/356/2009

MONTHLY ENVIRONMENTAL MONITORING & AUDIT REPORT

- AUGUST 2015 -

**CLIENTS:**

Civil Engineering and Development  
Department

and

Highways Department

**PREPARED BY:**

Lam Geotechnics Limited

11/F Centre Point  
181-185 Gloucester Road,  
Wanchai, H.K.

Telephone: (852) 2882-3939  
Facsimile: (852) 2882-3331  
E-mail: [info@lamenviro.com](mailto:info@lamenviro.com)  
Website: <http://www.lamenviro.com>

**CERTIFIED BY:**

Raymond Dai  
Environmental Team Leader

**DATE:**

11 September 2015

Ref.: AACWBIECEM00\_0\_7131L.15

14 September 2015

AECOM Asia Company Limited  
Engineer's Representative's Office  
25 Hung Hing Road,  
Causeway Bay,  
Hong Kong

By Post and Fax (3912 3010)

Attention: Mr. Peter Poon

Dear Mr. Poon,

**Re: Contract No. HK/2011/07  
Wan Chai Development Phase II - Central-Wan Chai Bypass  
Sampling, Field Measurement and Testing Works (Stage 2)**

**Monthly Environmental Monitoring and Audit Report (August 2015)  
for EP-356/2009, FEP-02/356/2009, FEP-03/356/2009, FEP-  
04/356/2009, FEP-06/356/2009 and FEP-07/356/2009**

Reference is made to the Environmental Team's submission of the captioned Monthly Environmental Monitoring and Audit (EM&A) Report for August 2015 received by e-mail on 11 September 2015 for our review and comment.

Please be informed that we have no adverse comment on the captioned submission. We write to verify the captioned submission in accordance with Condition 3.4 in the captioned Environmental Permits.

Thank you very much for your kind attention and please do not hesitate to contact the undersigned should you have any queries.

Yours sincerely,



David Yeung  
Independent Environmental Checker

Encl.

Q:\Projects\AACWBIECEM00\Corr\AACWBIECEM00\_0\_7131L.15.docx

C.c.

HyD

CEDD

AECOM

AECOM

Lam

Attn: Mr. Bond Chow

Attn: Mr. Jason Cheung

Attn: Mr. Frankie Fan

Attn: Mr. Conrad Ng

Attn: Mr. Raymond Dai

by fax: 2714 5289

by fax: 2577 5040

by fax: 2691 2649

by fax: 2691 2649

by fax: 2882 3331



**TABLE OF CONTENTS**

**EXECUTIVE SUMMARY ..... 4**

**1. INTRODUCTION..... 12**

1.1 Scope of the Report ..... 12

1.2 Structure of the Report..... 12

**2. PROJECT BACKGROUND..... 14**

2.1 Background ..... 14

2.2 Scope of the Project and Site Description ..... 14

2.3 Division of the Project Responsibility ..... 15

2.4 Project Organization and Contact Personnel..... 16

**3. STATUS OF REGULATORY COMPLIANCE ..... 21**

3.1 Status of Environmental Licensing and Permitting under the Project..... 21

**4. MONITORING REQUIREMENTS..... 32**

4.1 Noise Monitoring ..... 33

4.2 Air Monitoring ..... 34

4.3 Water Quality Monitoring..... 37

**5. MONITORING RESULTS ..... 42**

5.1 Noise Monitoring Results ..... 42

5.2 Real-time Noise Monitoring..... 44

5.3 Air Monitoring Results ..... 45

5.4 Water Monitoring Results..... 47

5.5 Waste Monitoring Results ..... 54

**6. COMPLIANCE AUDIT ..... 60**

6.1 Noise Monitoring ..... 61

6.2 Real-time noise Monitoring ..... 61

6.3 Air Monitoring ..... 61

6.4 Water Quality Monitoring..... 62

6.5 Review of the Reasons for and the Implications of Non-compliance..... 63

6.6 Summary of action taken in the event of and follow-up on non-compliance ..... 63

**7. CUMULATIVE CONSTRUCTION IMPACT DUE TO THE CONCURRENT PROJECTS ..... 64**

**8. ENVIRONMENTAL SITE AUDIT..... 65**

**9. COMPLAINTS, NOTIFICATION OF SUMMONS AND PROSECUTION ..... 68**

**10. CONCLUSION ..... 70**

## LIST OF TABLES

<b>Table I</b>	<b>Summary of Water Quality Monitoring Exceedances in Reporting Month</b>
<b>Table II</b>	<b>Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting Month</b>
<b>Table 2.1</b>	<b>Schedule 2 Designated Projects under this Project</b>
<b>Table 2.2</b>	<b>Details of Individual Contracts under the Project</b>
<b>Table 2.3</b>	<b>Contact Details of Key Personnel</b>
<b>Table 3.1</b>	<b>Summary of the current status on licences and/or permits on environmental protection pertinent to the Project</b>
<b>Table 3.2</b>	<b>Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/01</b>
<b>Table 3.3</b>	<b>Summary of submission status under FEP-02/356/2009 Condition</b>
<b>Table 3.4</b>	<b>Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/02</b>
<b>Table 3.5</b>	<b>Summary of submission status under FEP-03/356/2009 Condition</b>
<b>Table 3.6</b>	<b>Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/15</b>
<b>Table 3.7</b>	<b>Summary of submission status under FEP-04/356/2009 Condition</b>
<b>Table 3.8</b>	<b>Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/19</b>
<b>Table 3.9</b>	<b>Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08</b>
<b>Table 3.10</b>	<b>Summary of submission status under EP-356/2009 &amp; FEP-06/356/2009 Condition</b>
<b>Table 3.11</b>	<b>Cumulative Summary of Valid Licences and Permits under Contract no. HY/2010/08</b>
<b>Table 3.12</b>	<b>Summary of submission status under EP-356/2009 and FEP-07/356/2009 Condition</b>
<b>Table 4.1</b>	<b>Noise Monitoring Station</b>
<b>Table 4.2</b>	<b>Real Time Noise Monitoring Station</b>
<b>Table 4.3</b>	<b>Air Monitoring Station</b>
<b>Table 4.4</b>	<b>Marine Water Quality Stations for Water Quality Monitoring</b>
<b>Table 4.5</b>	<b>Marine Water Quality Monitoring Frequency and Parameters</b>
<b>Table 4.6</b>	<b>Marine Water Quality Stations for Enhanced Water Quality Monitoring</b>
<b>Table 5.1</b>	<b>Noise Monitoring Station for Contract nos. HK/2009/01, HK/2009/02</b>
<b>Table 5.2</b>	<b>Noise Monitoring Station for Contract no. HY/2009/15</b>
<b>Table 5.3</b>	<b>Noise Monitoring Station for Contract no. HY/2009/19</b>
<b>Table 5.4</b>	<b>Noise Monitoring Station for Contract no. HY/2010/08</b>
<b>Table 5.5</b>	<b>Real Time Noise Monitoring Station for Contract no. HY/2009/19</b>
<b>Table 5.6</b>	<b>Air Monitoring Station for Contract no. HK/2009/01</b>
<b>Table 5.7</b>	<b>Air Monitoring Station for Contract no. HK/2009/02</b>
<b>Table 5.8</b>	<b>Air Monitoring Station for Contract no. HY/2009/15</b>
<b>Table 5.9</b>	<b>Air Monitoring Stations for Contract no. HY/2009/19</b>
<b>Table 5.10</b>	<b>Air Monitoring Stations for Contract no. HK/2012/08</b>
<b>Table 5.11</b>	<b>Air Monitoring Stations for Contract no. HY/2010/08</b>
<b>Table 5.12</b>	<b>Water Monitoring Stations for contracts with respect to remaining DP3 work areas after the completion of DP5 &amp; DP6 in 2012 and intake diversion in 2013</b>
<b>Table 5.13</b>	<b>Water Monitoring Stations for Contract no. HK/2009/01</b>
<b>Table 5.14</b>	<b>Water Monitoring Stations for Contract no. HK/2009/02</b>
<b>Table 5.15</b>	<b>Water Monitoring Stations for Contract no. HK/2012/08</b>
<b>Table 5.16</b>	<b>Water Monitoring Stations for Contract no. HY/2009/15</b>
<b>Table 5.17</b>	<b>Summary of Water Quality Monitoring Exceedances in Reporting Month</b>
<b>Table 5.18</b>	<b>Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting Month</b>
<b>Table 5.19</b>	<b>Details of Waste Disposal for Contract no. HK/2009/01</b>
<b>Table 5.20</b>	<b>Details of Waste Disposal for Contract no. HK/2009/02</b>
<b>Table 5.21</b>	<b>Details of Waste Disposal for Contract no. HY/2009/15</b>
<b>Table 5.22</b>	<b>Details of Waste Disposal for Contract no. HY/2009/19</b>
<b>Table 5.23</b>	<b>Details of Waste Disposal for Contract no. HK/2012/08</b>
<b>Table 5.24</b>	<b>Details of Waste Disposal for Contract no. HY/2010/08</b>
<b>Table 8.1</b>	<b>Summary of Environmental Inspections for Contract no. HK/2009/01</b>

<b>Table 8.2</b>	<b><i>Summary of Environmental Inspections for Contract no. HK/2009/02</i></b>
<b>Table 8.3</b>	<b><i>Summary of Environmental Inspections for Contract no. HY/2009/15</i></b>
<b>Table 8.5</b>	<b><i>Summary of Environmental Inspections for Contract no. HK/2012/08</i></b>
<b>Table 8.6</b>	<b><i>Summary of Environmental Inspections for Contract no. HY/2010/08</i></b>
<b>Table 9.1</b>	<b><i>Cumulative Statistics on Complaints</i></b>
<b>Table 9.2</b>	<b><i>Cumulative Statistics on Successful Prosecutions</i></b>
<b>Table 10.1</b>	<b><i>Construction Activities and Recommended Mitigation Measures in Coming Reporting Month</i></b>

#### **LIST OF FIGURES**

<b>Figure 2.1</b>	<b><i>Project Layout</i></b>
<b>Figure 2.2</b>	<b><i>Project Organization Chart</i></b>
<b>Figure 4.1</b>	<b><i>Locations of Environmental Monitoring Stations</i></b>

#### **LIST OF APPENDICES**

<b>Appendix 3.1</b>	<b><i>Environmental Mitigation Implementation Schedule</i></b>
<b>Appendix 4.1</b>	<b><i>Action and Limit Level</i></b>
<b>Appendix 4.2</b>	<b><i>Copies of Calibration Certificates</i></b>
<b>Appendix 5.1</b>	<b><i>Monitoring Schedule for Reporting Month and Coming month</i></b>
<b>Appendix 5.2</b>	<b><i>Noise Monitoring Results and Graphical Presentations</i></b>
<b>Appendix 5.3</b>	<b><i>Air Quality Monitoring Results and Graphical Presentations</i></b>
<b>Appendix 5.4</b>	<b><i>Water Quality Monitoring Results and Graphical Presentations</i></b>
<b>Appendix 5.5</b>	<b><i>Real-time Noise Monitoring Results and Graphical Presentations</i></b>
<b>Appendix 6.1</b>	<b><i>Event Action Plans</i></b>
<b>Appendix 6.2</b>	<b><i>Summary for Notification of Exceedance</i></b>
<b>Appendix 9.1</b>	<b><i>Complaint Log</i></b>
<b>Appendix 10.1</b>	<b><i>Construction Programme of Individual Contracts</i></b>

## **EXECUTIVE SUMMARY**

- i. This is the Environmental Monitoring and Audit (EM&A) Monthly Report – [August 2015](#) for the Project of Wan Chai Development Phase II and Central-Wanchai Bypass under Environmental Permit no. EP-356/2009 and Further Environmental permit nos. FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009 and FEP-07/356/2009. This report presents the environmental monitoring findings and information recorded during the period [July 2015 to August 2015](#). The cut-off date of reporting is at 27<sup>th</sup> of each reporting month.

### Construction Activities for the Reported Period

- ii. During this reporting period, the major work activities for Contract no. HK/2009/01 included:
- Nil
- iii. During this reporting period, the major work activities for Contract no. HK/2009/02 included:
- [Placing levelling stone for construction of seawall at WCR3](#)
  - [Rock filling works at WCR3](#)
- iv. During this reporting period, the major work activities for Contract no. HY/2009/15 included:
- [Reinstatement of vertical seawall at TPCWAE](#)
- v. During this reporting period, the major work activities for Contract no. HY/2009/19 included:
- Nil
- vi. During this reporting period, the major work activities for Contract no. HK/2012/08 included:
- [Dry dock construction](#)
  - [Installation of pipe pile wall](#)
  - [Removal of temporary piling platform for culvert diversion](#)
  - [Construction of culvert](#)
- vii. During this reporting period, the major work activities for Contract no. HY/2010/08.
- [Diversion pipe maintenance](#)

### Noise Monitoring

- viii. [No action and limit level exceedance was recorded in this reporting month.](#)
- ix. Noise monitoring during daytime and restricted hour were conducted at the stations M1a, M2b, M3a, M4b, M5b and M6 on a weekly basis in the reporting month.

### Real-time Noise Monitoring

- x. As the land-based piling and filling works- DP3 at Tin Hau had been completed on 3 September 2012 and confirmed by RSS, the real-time noise monitoring results at RTN1 -

- FEHD Hong Kong Transport Section Whitfield Depot was excluded under EP-356/2009 since 28 November 2012.
- xi. The real-time noise monitoring at RTN2-Oil Street Community Liaison Centre has been relocated to City Garden Electric Centre (RTN2a- Electric Centre) on 5 Oct 2012, which is a representative of noise sensitive receiver- City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted in Electric Centre from 4 December 2009 to 17 December 2009.
  - xii. 24-hour real time noise monitoring was conducted at RTN2a – Hong Kong Electric Centre. No limit level exceedance was recorded in the reporting month.

#### Air Quality Monitoring

- xiii. Due to electricity interruption, the 24hr and 1 hr TSP monitoring of the following stations were rescheduled as below:  
24hr TSP for CMA1b was rescheduled from 28 July 2015 and 26 August 2015 to 29 July 2015 and 27 August 2015 respectively.  
24hr TSP for CMA6a was rescheduled from 26 August 2015 to 29 August 2015.  
1hr TSP for CMA6a was rescheduled from 27 August 2015 to 28 August 2015.
- xiv. One action level exceedance during 24hr TSP monitoring was recorded at monitoring station CMA2a – Causeway Bay Community Centre on 26 August 2015 in the reporting month. Investigation found that the exceedance recorded was not related to the Project.
- xv. Two action level exceedances during 1hr TSP monitoring was recorded at monitoring station CMA2a – Causeway Bay Community Centre on 27 August 2015 in the reporting month. Investigation found that the exceedance recorded was not related to the Project.
- xvi. The odour patrol along the odour route with 7 sniffing locations was conducted by a qualified odour patrol member on 4 and 18 August 2015 at the concerned hours (afternoon for higher daily temperature). No Action and Limit Level was recorded during this reporting month.
- xvii. With respect to the area handover, the air quality monitoring station CMA5a at Children Playgrounds opposite to the Pedestrian Plaza was relocated to the Pedestrian Plaza on 3 December 2014. The station reference and location ID of the air quality monitoring station CMA5a was updated as CMA5b and Pedestrian Plaza respectively
- xviii. Due to extension of site boundary by contractor of HY/2009/19, location of air monitoring station CMA1b – Oil Street Community Liaison Centre has been finely adjusted on 21 April 2012.
- xix. The location ID of air monitoring station CMA1b was updated as Oil Street Site Office in April 2013.
- xx. 1-hour and 24-hour Total Suspended Particulates (TSP) monitoring were conducted at CMA1b – Oil Street Site Office; CMA2a – Causeway Bay Community Center; CMA3a – CWB PRE Site Office Area; CMA4a – Society for the Prevention of Cruelty to Animals; CMA5b – Pedestrian Plaza; CMA6a – WDII PRE Site Office.

#### Water Quality Monitoring

- xxi. Action and Limit level of water quality monitoring was transited from dry season to wet season from 1 April 2015.

- xxii. With respect to the construction stage and access condition at Ex-PCWAW and the potential DO concern within the area, the suspended Enhance DO monitoring within Ex-PCWAW area at the Enhance DO monitoring station Ex-PCWA-SE was resumed on 10 August 2015 at the finely adjusted monitoring location.
- xxiii. With respect to the construction works undertaken at Ex-PCWAW and the forthcoming wet season DO concern, the suspended Enhance DO monitoring within Ex-PCWAW area at the Enhance DO monitoring station Ex-PCWA-SW was resumed on 30 March 2015 at the finely adjusted monitoring location.
- xxiv. With respect to the commencement of seawall modification works at Ex-PCWAE and the location of the Enhance DO monitoring stations would form an active construction area, the Enhance DO monitoring at monitoring station EX-PCWA SW and SE were temporarily suspended from 2 March 2015 ebb tide and the monitoring at the location is tentatively to be resumed by early April 2015 to cater for the potential DO concern during Wet Season.
- xxv. As informed by CWB RSS, the operation of the diverted Windsor House cooling intake was commenced on 20 Dec 2014 and the water quality monitoring at monitoring station C7 for Windsor House Cooling water intake was resumed on 22 Dec 2014.
- xxvi. With respect to the commencement of temporary reclamation works and seawall construction at Ex-PCWAW zone and diverted culvert extension, the location of the Enhance DO monitoring stations (Ex-PCWASW and Ex-PCWA SE) were finely adjusted to the PCWAE since 7 November 2014.
- xxvii. With respect to the commencement of marine dredging works at WCR3 under contract HK/2009/02. The respective water quality monitoring station C1 were associated with HK/2009/01 and HK/2009/02.
- xxviii. As confirmed by CWB RSS, the operation of the pump station for Windsor House Cooling Water was suspended from 22 Oct 2014 for the Windsor House intake cooling intake scheme and temporary supply of freshwater from WSD water mains was provided to cooling water intake. The water quality monitoring for the respective cooling water intake at WQM station C7 was temporarily suspended from 22 Oct 2014.
- xxix. With respect to the commencement of filling works at TS3 and the formation of TZ3 reclamation zone, the enhance DO monitoring at Enhance monitoring station C7 was temporarily suspended from 22 Oct 2014.
- xxx. As confirmed by WDII RSS and IEC, the cross harbor dredging works have completed since 16 March 2012 while the dredging works for submarine outfall pipeline has completed since 29 November 2011, considering current construction stage and dredging Scenario, the water quality monitoring at stations WSD9 and WSD17 was temporarily suspended since 8 September 2014 flood tide.
- xxxi. With respect to the switching over of cooling water intake location, the water quality monitoring at the relocated intake station RW21-P789 under HK/2009/02 was commenced since 29 July 2013 and monitoring station C5e and C5w were temporarily suspended and switched over to monitoring station RW21-P789 on 29 July 2013 due to suspension of pump house operation.
- xxxii. As advised by WDII RSS, the water quality monitoring for WSD21 pump station with respect to HK/2009/02 was switched over to the relocated location since 12 March 2014. According to the EM&A Manual, the water quality monitoring station WSD21 was relocated to station RW21-P789 and the water quality monitoring at station WSD21 was temporarily suspended since 12 March 2014.

- xxxiii. With respect to the commencement of marine dredging works under contract HY/2010/08. The respective water quality monitoring station C7 were associated with HY/2009/15 and HY/2010/08.
- xxxiv. With respect to the commencement of marine dredging works under contract HK/2012/08/ The respective water quality monitoring station WSD19, P1, P3, P4, and P5 were associated with Contract HK/2012/08 Since September 2013.
- xxxv. WQM events on 22 April 2013 at monitoring stations C2, C3, C4e and C4w were temporarily suspended. Upon confirmation with WDII RSS and the IEC, water quality monitoring at relocated intakes monitoring location P1, P3, P4 and P5 were commenced since 24 April 2013.
- xxxvi. Due to the marine piling under Contract no. HY/2009/19 was completed on 4 March 2013, the temporary suspension of impact water quality monitoring at C8 and C9 from 4 March 2013 have been monitored for 4-week period after the completion of marine works to confirm no water deterioration.
- xxxvii. As confirmed by CWB RSS, the marine piling works under contract HY/2009/19 was confirmed completed by 4 March 2013. The water quality monitoring at the respective monitoring stations C8 and C9 were temporarily suspended since 30 March 2013.
- xxxviii. RSS confirmed that all Type III Dredging works under HK/2009/01 have been completed since Oct 2012.
- xxxix. Due to the presence of obstacle within the inner silt curtain frame at sampling point, water quality point at C7 was finely adjusted to the outside of the inner silt curtain frame since 29 Dec 2012.
- xl. With respect to the trial dredging at WCR2 was scheduled on 20, 22, 24, 25 March and 1, 3, 11, 13, 15, 17, 19, 20 Apr and 3 May 2012, on-going water quality monitoring results at WSD21 during this period was checked and indicated that there was no contribution due to the trial dredging operation. Enhanced review of water quality around WCR2 was also implemented and no deterioration in the water quality was observed.
- xli. Due to the access of water monitoring station at WSD19 was blocked by LCSD construction works from 3 April 2012 to 2 May 2012 and lead to the inaccessibility of sampling either land and marine, there is a fine adjustment of the sampling point of WSD 19 since 5 April 2012 to the closest accessible point prior to the completion of the construction activities.
- xlii. WDII/RSS advised that the dredging works for submarine pipeline at Victoria Harbour had been completed in January 2012. Therefore, the concurrent dredging activities at Sewage Pipeline Zone and reclamation shoreline zone TCBR under the EP-356/2009 scenario 2B no longer exist. As such, with reference to Table 5.39 of the EIA Report for Wan Chai Development Phase II and Central-Wan Chai Bypass, the application of silt screen for cooling water intakes for Queensway Government Offices was suspended and the others remain unchanged.
- xliii. Due to the dredging works for Cross Harbour Water Mains from Wan Chai to Tsim Sha Tsui-DP6 was completed on 26 March 2012, the temporary suspension of impact water quality monitoring at WSD7 and WSD20 after 27 April 2012 for the water quality monitoring at WSD7 and WSD20 have been monitored for 4-week period after the completion of DP6 to confirm no water deterioration. Water quality monitoring at WSD10 and WSD15 was temporary suspended while water quality monitoring at WSD9 and WSD17 was implemented with respect to HK/2009/02 from 8 Feb 12 onwards;

- xliv. Based on the joint inspection on 4 Jan 2012 for the NPR area, the 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8, C9 to confirm no water deterioration with respect to NPR was commenced since 7 Jan 2012 and it was completed on 6 February 2012.
- xliv. Based on the safety concern when external façade refurbishment was conducted by contractor employed by Provident Centre (C9) between 9 January 2012 to 30 July 2012 which caused to the inaccessibility of sampling either land and marine since 3 Feb 2012, there is a fine adjustment of the sampling location of water quality monitoring at C9 since 10 March 2012 to the closest accessible point prior to the completion of the external façade refurbishment work.
- xlvi. Water quality monitoring at C8 and C9 have been implemented with respect to HY/2009/19 since the marine bore piling work started on 28 Jan 12.

**Table I Summary of Water Quality Monitoring Exceedances in Reporting Month**

Contract no.	Water Monitoring Station	Mid-flood						Mid-ebb					
		DO		Turbidity		SS		DO		Turbidity		SS	
		AL	LL	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
HK/2009/01 & HK/2009/02	C1	0	0	0	0	0	0	0	0	0	0	0	0
HK/2012/08	WSD19	0	0	0	0	0	0	0	0	0	0	0	0
	P1	0	0	0	0	0	0	0	0	0	0	0	0
	P3	0	0	0	0	0	0	0	0	0	0	0	0
	P4	0	0	0	0	0	0	0	0	0	0	0	0
	P5	0	0	0	0	0	0	0	0	0	0	0	0
HK/2009/02	RW21-P789	0	0	0	0	0	0	0	0	0	0	0	0
HY/2009/15 & HY/2010/08	C7	0	0	0	0	0	0	0	0	0	0	0	0
<b>Total</b>		0	0	0	0	0	0	0	0	0	0	0	0

- Remarks: - The cessation of seawater intake operation for C6 was confirmed on 17 May 2011, the water monitoring at C6 was then terminated since 17 May 2011.
- WSD9 and WSD17 were implemented with respect to HK/2009/02 from 8 Feb 2012.
  - 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8 and C9 were completed on 6 Feb 2012.
  - C8 and C9 were implemented with respect to HY/2009/19 from 28 Jan 2012.
  - C8 & C9 was temporary suspended on 30 March 2013 due to the marine works for Contract no. HY/2009/19 had been completed on 4 March 2013
  - WSD7 and WSD20 water quality monitoring were temporarily suspended from 27 Apr 2012.
  - C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since 24 Apr 2013
  - C5e and C5w water quality monitoring station was temporarily suspended since 29 July 2013
  - WSD21 water quality monitoring station was temporarily suspended since 12 March 2014
  - Maintenance responsibility of silt screen C1, WSD19, P3, P4 and P5 are under Contract HK/2009/01.
  - WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 September 2014 flood tide.
  - Water quality monitoring for Windsor House Cooling (Station Ref: C7) was temporarily suspended since 22 October 2014 with respect to the diversion scheme and was resumed since 22 December 2014.
  - The water monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.

- xlvii. There was no action and no limit level of turbidity exceedance recorded in the reporting month.
- xlviii. Enhanced DO monitoring at 4 monitoring stations in Causeway Bay Typhoon Shelter and Ex-Public Cargo Works Area was conducted three days per week during the reporting period. The action and limit level exceedances of water quality monitoring are summarized in **Table II**.

**Table II Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting Month**

Contract no.	Water Monitoring Station	Mid-flood		Mid-ebb	
		DO		DO	
		AL	LL	AL	LL
HY/2009/15	C6	0	0	0	0
	C7	0	0	0	0
	Ex-WPCWA SW	0	1	0	5
	Ex-WPCWA SE	2	0	2	1
Total		2	1	2	6

- xlix. There were 4 action level and 7 limit level exceedances of enhanced dissolved oxygen recorded in this reporting month. Investigation found that the exceedances were not related to Project works. The details of the recorded exceedances can be referred to the **Section 6.4**.
  - i. In response to the Condition 2.18 of the Environmental Permit no. EP-356/2009 requiring that a silt curtain / impermeable barrier system be installed to channel water discharge flow from Culvert L to locations outside the embayment area, a proposed replacement of the requirement with additional dissolved oxygen monitoring has been conducted at three monitoring stations, namely A, B and C between the eastern seawall of Central Reclamation Phase III and the HKCEC Extension since November 2011 under EP-356/2009 so that DO level between the eastern seawall of Central Reclamation Phase II and the HKCEC extension could be continuously monitored.
  - ii. With respect to the commencement of dredging works under HK/2012/08 and the installation of MTR precast protection unit, the enhanced water quality monitoring for Culvert L was temporarily suspended since 24 July 2013.
  - iii. With respect to the commencement of filling works at TS3 and the formation of TZ3 reclamation zone, the enhance DO monitoring at Enhance monitoring station C7 was temporarily suspended from 22 Oct 2014.
  - liii. With respect to the commencement of temporary reclamation works and seawall construction at Ex-PCWAW zone and diverted culvert extension, the location of the Enhance DO monitoring stations (Ex-PCWASW and Ex-PCWA SE) were finely adjusted to the PCWAE since 7 November 2014.

Complaints, Notifications of Summons and Successful Prosecutions

- liv. No environmental complaint was received in this reporting month.

#### Site Inspections and Audit

- iv. The Environmental Team (ET) conducted weekly site inspections for Contract nos. HK/2009/01, HK/2009/02, HY/2009/15, HY/2009/19, HK/2012/08 and HY/2010/08 under EP no. EP-356/2009 in the reporting month. Major observations and recommendations made during the audit sessions were rectified by the Contractors. No non-conformance was identified during the site inspections.
- lvi. Construction works under HK/2010/06 was confirmed completed and the respective work area under FEP-05/356/2009 was handover and inspected under HK/2012/08 from 22 September 2014 onwards.

#### Future Key Issues

- lvii. In coming reporting month, the principal work activities of individual contracts are anticipated as follows:

##### [Contract no. HK/2009/01 – Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC](#)

- Nil

##### [Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East](#)

- Construction of Seawall At WCR3
- Reclamation at WCR3
- Demolition of remaining part of existing Wan Chai Ferry Pier

##### [Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel \(Causeway Bay Typhoon Shelter Section\)](#)

- Reinstatement of vertical seawall at TPCWAE

##### [Contract no. HY/2009/19- Wan Chai Bypass Tunnel \(North Point Section\) and Island Eastern Corridor Link](#)

- Nil

##### [Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West](#)

- Dry dock construction
- Installation of pipe pile wall
- Removal of temporary piling platform for culvert diversion
- Construction of culvert



Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8)

- Diversion pipe maintenance

## 1 Introduction

### 1.1 Scope of the Report

- 1.1.1. Lam Geotechnics Limited (LGL) has been appointed to work as the Environmental Team (ET) under Environmental Permit no. EP-356/2009 and Further Environmental permit nos. FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009 and FEP-07/356/2009 to implement the Environmental Monitoring and Audit (EM&A) programme as stipulated in the EM&A Manual of the approved Environmental Impact Assessment (EIA) Report for Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) and in the EM&A Manual of the approved EIA Report for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001).
- 1.1.2. This report presents the environmental monitoring and auditing work carried out in accordance to the Section 10.3 of EM&A Manual and “*Environmental Monitoring and Audit Requirements*” under Particular Specification Section 27.
- 1.1.3. This report documents the finding of EM&A works for Environmental Permit no. EP-356/2009, Further Environmental Permit no. FEP-02/356/2009, FEP-03/356/2009, FEP-04/356/2009, FEP-06/356/2009 and FEP-07/356/2009 during the period of [July 2015 to August 2015](#). The cut-off date of reporting is at 27<sup>th</sup> of each reporting month.

### 1.2 Structure of the Report

- Section 1**     *Introduction* – details the scope and structure of the report.
- Section 2**     *Project Background* – summarizes background and scope of the project, site description, project organization and contact details of key personnel during the reporting period.
- Section 3**     *Status of Regulatory Compliance* – summarizes the status of valid Environmental Permits / Licenses during the reporting period.
- Section 4**     *Monitoring Requirements* – summarizes all monitoring parameters, monitoring methodology and equipment, monitoring locations, monitoring frequency, criteria and respective event and action plan and monitoring programmes.
- Section 5**     *Monitoring Results* – summarizes the monitoring results obtained in the reporting period.
- Section 6**     *Compliance Audit* – summarizes the auditing of monitoring results, all exceedances environmental parameters.
- Section 7**     *Cumulative Construction Impact due to the Concurrent Projects* – summarizes the relevant cumulative construction impact due to the concurrent activities of the concurrent Projects.



- Section 8**     **Environmental Site Audit** – summarizes the findings of weekly site inspections undertaken within the reporting period, with a review of any relevant follow-up actions within the reporting period.
- Section 9**     ***Complaints, Notification of summons and Prosecution*** – summarizes the cumulative statistics on complaints, notification of summons and prosecution
- Section 10**    ***Conclusion***

## 2 Project Background

### 2.1 Background

- 2.1.1. “Wan Chai Development phase II and Central-Wan Chai Bypass” and “Central-Wan Chai Bypass and Island Eastern Corridor Link” (hereafter called “the Project”) are Designed Project (DP) under the Environmental Impact Assessment Ordinance (Cap. 499) (EIAO). The Environmental Impact Assessment (EIA) Reports for Central-Wan Chai Bypass and Island Eastern Corridor Link (Register No. AEIAR-041/2001) and Wan Chai Development phase II and Central-Wan Chai Bypass (Register No.: AEIAR-125/2008) have been approved on 31 August 2001 and 11 December 2008 respectively.
- 2.1.2. The key purpose of Wan Chai Development Phase II (WDII) is to provide land at Wan Chai North and North Point for construction of the Central-Wan Chai Bypass and Island Eastern Corridor Link (CWB). Land formed under the project will be developed as a world-class waterfront promenade joining that at the new Central waterfront for public enjoyment.
- 2.1.3. There is a compelling and present need for the CWB to provide relief to the very congested east-west Connaught Road Central/Harcourt Road / Gloucester Road Corridor (the Corridor) which is currently operating beyond its capacity. The CWB will provide relief to the existing congestion along the Corridor and cater for the anticipated growth of traffic on Hong Kong Island. Without the CWB and its access roads, there will not be sufficient capacity to serve the heavy traffic demands at both strategic and local levels.

### 2.2 Scope of the Project and Site Description

- 2.2.1. The Project is located mainly in Wan Chai North, Causeway Bay and North Point, and is demarcated by Gloucester Road and Victoria Park Road to the south, Fenwick Pier Street to the west and Tong Shui Road Interchange to the east, as shown in **Figure 2.1**.
- 2.2.2. The study area encompasses existing developments along the Wan Chai, Causeway Bay and North Point shorelines. Major land uses include the Hong Kong Convention & Exhibition Centre (HKCEC) Extension, the Wan Chai Ferry Pier, the ex-Wan Chai Public Cargo Working Area (ex-PCWA), the Royal Hong Kong Yacht Club (RHKYC), the Police Officers’ Club, the Causeway Bay Typhoon Shelter (CBTS) and commercial and residential developments.
- 2.2.3. The scope of the Project comprises:
- Land formation for key transport infrastructure and facilities, including the Trunk Road (i.e. CWB) and the associated slip roads for connection to the Trunk Road and for through traffic from Central to Wan Chai and Causeway Bay. The land formed for the above transport infrastructure will provide opportunities for the development of an attractive waterfront promenade for the enjoyment of the public
  - Reprovisioning / protection of the existing facilities and structures affected by the land formation works mentioned above
  - Extension, modification, reprovisioning or protection of existing storm water drainage outfalls, sewerage outfalls and water mains affected by the revised land use and land formation works mentioned above

- Upgrading of hinterland storm water drainage system and sewerage system, which would be rendered insufficient by the land formation works mentioned above
- Provision of the ground level roads, flyovers, footbridges, necessary transport facilities and the associated utility services
- Construction of the new waterfront promenade, landscape works and the associated utility services
- The Trunk Road (i.e. CWB) within the study area and the associated slip roads for connection to the Trunk Road.

2.2.4. The project also contains various Schedule 2 DPs that, under the EIAO, require Environmental Permits (Eps) to be granted by the DEP before they may be either constructed or operated. **Table 2.1** summarises the five individual DPs under this Project. [Figure 2.1](#) shows the locations of these Schedule 2 DPs.

**Table 2.1 Schedule 2 Designated Projects under this Project**

Item	Designated Project	EIAO Reference	Reason for inclusion
DP1	Central-Wanchai Bypass (CWB) including its road tunnel and slip roads	Schedule 2, Part I, A.1 and A.7	Trunk road and road tunnel more than 800 m in length
DP2	Road P2 and other roads which are classified as primary/district distributor roads	Schedule 2, Part I, A.1	Primary / district distributor roads
DP3	Reclamation works including associated dredging works	Schedule 2, Part I, C.1 and C.12	Reclamation more than 5 ha in size and a dredging operation less than 100 m from a seawater intake point
DP5	Wan Chai East Sewage Outfall	Schedule 2, Part I, F.5 and F.6	Submarine sewage pipelines with a total diameter more than 1,200 mm and include a submarine sewage outfall
DP6	Dredging for the Cross-harbour Water Mains from Wan Chai to Tsim Sha Tsui	Schedule 2, Part I, C.12	A dredging operation less than 100 m from a seawater intake point

### 2.3 Division of the Project Responsibility

2.3.1. Due to the multi-contract nature of the Project, there are a number of contracts sub-dividing the whole works area into different work areas to be commenced. Contractors of individual contracts will be required by the EP holder to apply Further Environmental Permits (FEP) such that the impact monitoring stations are sub-divided accordingly to facilitate the implementation of EM&A programme and to streamline the EM&A reporting for individual FEP holders correspondingly.

2.3.2. The details of individual contracts are summarized in **Table 2.2**.

**Table 2.2 Details of Individual Contracts under the Project**

Contract No.	Contract Title	Associated DP(s)	Construction Commencement Date
HK/2009/01	Wan Chai Development Phase II – Central –Wanchai Bypass at Hong Kong Convention and Exhibition Centre	DP3, DP6	23 July 2010
		DP1, DP2	25 August 2011
HK/2009/02	Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East	DP3, DP5	5 July 2010
		DP1	26 April 2011
HY/2009/11	Wan Chai Development Phase II and Central – Wan Chai Bypass – North Point Reclamation	DP3	17 March 2010 (Completed)
HY/2009/15	Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)	DP3	10 November 2010
		DP1	13 July 2011
HK/2010/06	Wan Chai Development Phase II-Central-Wan Chai Bypass over MTR Tsuen Wan Line	DP3	22 March 2011 (Completed)
04/HY/2006	Reconstruction of Bus Terminus near Man Yiu Street and Man Kwong Street	DP1	September 2010 (Completed)
HY/2009/17	Central – Wan Chai Bypass (CWB) at FEHD Whitfield Depot – Advanced piling works.	DP1	5 October 2010 (Completed)
HY/2009/18	Central – Wan Chai Bypass (CWB) – Central Interchange	DP1	21 April 2011
HY/2009/19	Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link	DP1	24 March 2011
HK/2012/08	Wan Chai Development Phase II Central-Wan Chai Bypass at Wan Chai West	DP1,DP2, DP3	10 March 2014
HY/2010/08	Central- Wanchai Bypass Tunnel – Tunnel (Slip Road 8)	DP1, DP2, DP3	21 March 2013
HY/2011/08	Central-Wan Chai Bypass (CWB) – Tunnel Buildings, Systems and Fittings, and Works Associated with Tunnel Commissioning	DP1	8 October 2014

## 2.4 Project Organization and Contact Personnel

- 2.4.1. Civil Engineering and Development Department and Highways Department are the overall project controllers for the Wan Chai Development Phase II and Central-Wan Chai Bypass respectively. For the construction phase of the Project, Project Engineer, Contractor(s), Environmental Team and Independent Environmental Checker are appointed to manage and control environmental issues.
- 2.4.2. The proposed project organization and lines of communication with respect to environmental protection works are shown in **Figure 2.2**. Key personnel and contact particulars are summarized in **Table 2.3**:

**Table 2.3 Contact Details of Key Personnel**

Party	Role	Post	Name	Contact No.	Contact Fax
AECOM	Engineer's Representative for WDII	Principal Resident Engineer	Mr. Frankie Fan	2587 1778	2587 1877
	Engineer's Representative for CWB	Principal Resident Engineer	Mr. Peter Poon	3912 3388	3912 3010
Chun Wo – Leader Joint Venture	Contractor under Contract no. HK/2009/01	Project Manager	Mr. Simon Liu	9304 8355	2587 1878
		Site Agent	Mr. Andy Yu	9648 4896	
		Engineer Manager	Mr. Terry Wong	9757 9846	
		Construction Manager	Mr. Wyman Wong	9627 2467	
		Construction Manager	Mr. Kenneth Chan	9160 3850	
		Environmental Officer	Ms. Wendy Ng	9803 0057	
		Assistant Environmental Engineer	Miss. Connie Chan	6157 7057	
Chun Wo – CRGL Joint Venture	Contractor under Contract no. HK/2009/02	Project Manager	Mr. Paul Yu	3658-3085	2827 9996
		Quality & Environmental Manager	Mr. C.P. Ho	9191 8856	
China State Construction Engineering (HK) Ltd.	Contractor under Contract no. HY/2009/15	Project Director	Chris Leung	3557 6393	2566 2192
		Site Manager	Y Huo	3557 6368	
		Contractor's Representative	Andrew Wong	3557 6371	
		Contractor's Representative	Gene Cheung	3557 6395	
		Environmental Officer	Andy Mak	3557 6347	
Chun Wo – CRGL – MBEC Joint Venture	Contractor under Contract no. HY/2009/19	Project Manager	David Lau	3758 8879	2570 8013
		Site Agent	Paul Yu	9456 9819	
		Deputy Site Agent	Eric Fong	6191 9337	
		Environmental Manager / Environmental Officer	M.H. Isa	9884 0810	
		Construction Manager (Marine)	Andy Chan	9879 4325	
		Construction Manager (Land)	Bear Ding	6483 6198	
		Operation Manager (Land)	Yung Kwok Wah	9834 1010	
China	Contractor	Project Director	C. N. Lai	9106 5806	2877 1522

Party	Role	Post	Name	Contact No.	Contact Fax
State- Leader JV	under Contract no. HK/2012/08	Project Manager	Eddie Chung	9189 8118	
		Site Agent	Keith Tse	9037 1839	
		Environmental Officer	James Ma	9130 9549	
		Environmental Supervisor	Y. L. Ho	9856 5669	
China State	Contractor under Contract no. HY/2010/08	Project Director	Chris Leung	3467 4299	2566 8061
		Project Manager	Chan Ying Lun	3418 3001	
		Site Agent	Dave Chan	3467 4277	
		Environmental Officer	Gabriel Wong	35576466	
		Environmental Supervisor	Desmond Ho Tsz Ho	3557 6466	
Leighton Joint Venture	Contractor under Contract no. HY/2011/08	Project Manager	Paul Evans	2823 1111	21406799
		Site Agent	Colman Wong	9730 0806	
		Environmental Officer	David Hung	9765 6161	
		Environmental Supervisor	Penny Yiu	2214 7738	
Ramboll Environ Hong Kong Limited	Independent Environmental Checker (IEC)	Independent Environmental Checker (IEC)	Mr. David Yeung	3465 2888	3465 2899
Lam Geotechni cs Limited	Environmental Team (ET)	Environmental Team Leader (ETL)	Mr. Raymond Dai	2882 3939	2882 3331

2.4.3. For Contract no. HK/2009/01, the principal work activities in this reporting month included:

- Nil

2.4.4. For Contract no. HK/2009/02, the principal work activities in this reporting month included:

- Placing levelling stone for construction of seawall at WCR3
- Rock filling work at WCR3

2.4.5. For Contract no. HY/2009/15, the principal work activities in this reporting month included:

- Reinstatement of vertical seawall at TPCWAE

2.4.6. For Contract no. HY/2009/19, the principal work activity in this reporting month included:

- Nil

2.4.7. For Contract no. HK/2012/08, the principal work activity in this reporting month included:

- Dry dock construction
- Installation of pipe pile wall
- Removal of temporary piling platform for culvert diversion
- Construction of culvert

2.4.8. For Contract no. HY/2010/08, no principal work activities this reporting month.

- Diversion pipe maintenance

2.4.9. In coming reporting month, the principal work activities of individual contracts are anticipated as follows:

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

- Nil

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East

- Construction of seawall at WCR3
- Reclamation at WCR3
- Demolition of remaining part of existing Wan Chai Ferry Pier

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

- Reinstatement of vertical seawall at TPCWAE

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- Nil

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

- Dry dock construction
- Installation of pipe pile wall



- Removal of temporary piling platform for culvert diversion
- Construction of culvert

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8)

- Diversion pipe maintenance

### 3 Status of Regulatory Compliance

#### 3.1 Status of Environmental Licensing and Permitting under the Project

3.1.1. A summary of the current status on licences and/or permits on environmental protection pertinent to the Project is shown in **Table 3.1**.

**Table 3.1 Summary of the current status on licences and/or permits on environmental protection pertinent to the Project**

Permits and/or Licences	Reference No.	Issued Date	Status
Environmental Permit	EP-356/2009	30 Jul 2009	Valid
Environmental Permit	EP-364/2009	17 Aug 2009	Superseded
Environmental Permit	EP-364/2009/A	4 Aug 2010	Superseded
Environmental Permit	EP-364/2009/B	20 Sep 2012	Superseded
Environmental Permit	EP-364/2009/C	11 Jul 2014	Valid
Environmental Permit	EP-376/2009	13 Nov 2010	Valid
Further Environmental Permit	FEP-01/356/2009	18 Feb 2010	Surrendered
Further Environmental Permit	FEP-02/356/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-03/356/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-04/356/2009	22 Nov 2010	Valid
Further Environmental Permit	FEP-05/356/2009	24 Mar 2011	Surrendered
Further Environmental Permit	FEP-01/364/2009	24 Mar 2010	Valid
Further Environmental Permit	FEP-02/364/2009	21 Apr 2010	Valid
Further Environmental Permit	FEP-03/364/2009	12 Jul 2010	Surrendered
Further Environmental Permit	FEP-04/364/2009/A	14 Oct 2010	Surrendered
Further Environmental Permit	FEP-05/364/2009/A	15 Nov 2010	Valid
Further Environmental Permit	FEP-06/364/2009/A	22 Nov 2010	Valid
Further Environmental Permit	FEP-07/364/2009/B	20 Sep 2012	Valid
Further Environmental Permit	FEP-08/364/2009/A	15 Jun 2012	Surrendered
Further Environmental Permit	FEP-06/356/2009	5 Mar 2013	Valid
Further Environmental Permit	FEP-07/356/2009	26 July 2013	Valid
Further Environmental Permit	FEP-09/364/2009/B	5 March 2013	Valid
Further Environmental Permit	FEP-10/364/2009/B	26 July 2013	Valid

Permits and/or Licences	Reference No.	Issued Date	Status
Further Environmental Permit	FEP-11/364/2009/B	2 May 2014	Valid

3.1.2. Due to the multi-contract nature of the Project, the status of permits and/or licences under the individual contract(s) are presented as below:

Contract no. HK/2010/06 – Wan Chai Development Phase II – Central – Wan Chai Bypass over MTR Tsuen Wan Line under FEP-05/356/2009

3.1.3. The construction works were completed and the FEP-05/356/2009 was surrendered by the Contractor on 3 October 2014.

Contract no. HK/2009/01 – Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

3.1.4. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HK/2009/01 under FEP-02/356/2009 are shown in **Table 3.2** and **Table 3.3**.

**Table 3.2 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/01**

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-02/356/2009	24 Mar 2010	N/A	Valid
	FEP-02/364/2009	21 Apr 2010	N/A	Valid
Notification of Works Under APCO	313088	06 Jan 2010	N/A	Valid
Construction Noise Permit (CNP) for non-piling equipment	GW-RS0079-15	27 Jan 2015	16 Feb 2015 to 14 Aug 2015	Expired
	GW-RS0104-15	3 Feb 2015	22 Feb 2015 to 21 Aug 2015	Expired
	GW-RS0101-15	3 Feb 2015	22 Feb 2015 to 21 Aug 2015	Expired
	GW-RS0074-15	22 Jan 2015	10 Feb 2015 to 9 Aug 2015	Expired
	GW-RS0243-15	16 Mar 2015	25 Mar 2015 to 24 Sept 2015	Valid
	GW-RS-269-15	16 Mar 2015	8 Apr 2015 to 7 Oct 2015	Valid
	GW-RS0408-15	13 Apr 2015	20 Apr 2015 to 19 Oct 2015	Cancelled

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	GW-RS0416-15	16 Apr 2015	8 May 2015 to 7 Nov 2015	Valid
	GW-RS0445-15	30 Apr 2015	26 May 2015 to 25 Nov 2015	Valid
	GW-RS0462-15	30 Apr 2015	2 May 2015 to 1 Nov 2015	Valid
	GW-RS0706-15	30 Jun 2015	2 Jul 2015 to 1 Jan 2016	Valid
	GW-RS0803-15	28 Jul 2015	21 Aug 2015 to 20 Feb 2016	Valid
	GW-RS0804-15	28 Jul 2015	22 Aug 2015 to 21 Feb 2016	Valid
	GW-RS0868-15	13 Aug 2015	14 Aug 2015 to 13 Feb 2016	Valid
Discharge Licence	WT00021138-2015	13 Apr 2015	31 Mar 2020	Valid
	WT00009641-2011	24 Jul 2011	31 Jul 2016	Valid
Billing account under Waste Disposal Ordinance	7010069	21 Jan 2010	N/A	Valid
Registration as a Chemical Waste Producer	WPN5213-134-C3585-01	21 Jan 2010	N/A	Valid
Dumping Permit (Type 1 – Open Sea Disposal)	EP/MD/16-018	2 Jun 2015	6 Jun 2015 to 30 Sept 2015	Cancelled
	EP/MD/16-062	17 Aug 2015	18 Aug 2015 to 30 Sept 2015	Valid
Dumping Permit (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal)	EP/MD/16-046	15 Jul 2015	20 Jul 2015 to 19 Aug 2015	Expired

**Table 3.3 Summary of submission status under FEP-02/356/2009 Condition**

EP Condition	Submission	Date of Submission
Condition 2.6	Management Organization of Main Construction Companies	13 Apr 2010

EP Condition	Submission	Date of Submission
Condition 2.7	Works Schedule and Location Plan	8 Apr 2010
Condition 2.8	Silt Curtain Deployment Plan (Rev. 5)	24 Aug 2012
	Silt Curtain Deployment Plan (Rev. 4)	12 July 2012
	Silt Curtain Deployment Plan (Rev. 3)	27 June 2012
	Silt Curtain Deployment Plan	19 Apr 2010
Condition 2.9	<a href="#">Silt Screen Deployment Plan (Rev. 8)</a>	<a href="#">28 Aug 2015</a>
	Silt Screen Deployment Plan (Rev. 7)	21 Nov 2014
	Silt Screen Deployment Plan (Rev. 6)	20 Aug 2014
	Silt Screen Deployment Plan (Rev.5)	24 Jul 2013
	Silt Screen Deployment Plan (Rev.4)	15 Nov 2012
	Silt Screen Deployment Plan	19 Apr 2010
Conditions 2.8 and 2.9	Supplementary Document on Silt Curtain and Silt Screen Deployment Plan	19 Jul 2010
	Report on Field Testing for Silt Curtain	26 Aug 2010
	Report on Field Testing for Silt Curtain (Rev. A)	15 Nov 2010
Condition 2.12(d)	Alternative Proposal on Concurrent Dredging for Sewage Pipeline and Cross Harbour Water Mains	15 Apr 2011
Condition 2.17	Noise Management Plan	23 Apr 2010
Condition 2.18	Landscape Plan (Erection of Decorative Screen Hoarding along Construction Site around Hong Kong Exhibition and Convention Centre)	15 May 2010
	Landscape Plan (Night-time Lighting)	22 Oct 2010
	Landscape Plan (Rev. B)	15 Nov 2010
Condition 1.12	Notification of Commencement Date	20 Jun 2011
Condition 2.6 to 2.8	Management Organization, Works Schedule and Location Plan	18 May 2011
Condition 2.9	Silt Screen Deployment Plan	10 Jun 2011
Condition 2.18	Landscape Plan	31 Oct 2013

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

3.1.5. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HK/2009/02 under FEP-03/356/2009 are shown in **Table 3.4** and **Table 3.5**.

**Table 3.4 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2009/02**

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-03/356/2009	24 Mar 2010	N/A	Valid
	FEP-01/364/2009	24 Mar 2010	N/A	Valid
Notification of Works Under APCO	313962	2 Feb 2010	N/A	Valid
Construction Noise Permit (CNP) for non-piling equipment	GW-RS0085-15	27 Jan 2015	14 Feb 2015 to 13 Aug 2015	Expired
	GW-RS0198-15	24 Feb 2015	26 Feb 2015 to 22 Aug 2015	Expired
	GW-RS0236-15	13 Mar 2015	25 Mar 2015 to 24 Sep 2015	Valid
	GW-RS0246-15	13 Mar 2015	22 Mar 2015 to 13 Sep 2015	Valid
	GW-RS0446-15	30 April 2015	27 May 2015 to 26 Nov 2015	Valid
	GW-RS0447-15	30 April 2015	22 May 2015 to 21 Nov 2015	Valid
	GW-RS0454-15	30 April 2015	2 May 2015 to 28 Oct 2015	Valid
	GW-RS0454-15	30 April 2015	2 May 2015 to 29 Oct 2015	Valid
	GW-RS0544-15	22 May 2015	26 May 2015 to 18 Nov 2015	Valid
	GW-RS0610-15	10 Jun 2015	22 Jun 2015 to 21 Dec 2015	Valid
	GW-RS0637-15	11 Jun 2015	18 Jun 2015 to 8 Dec 2015	Valid
	GW-RS0709-15	30 June 2015	2 Jul 2015 to 1 Jan 2016	Valid
	GW-RS0716-15	30 June 2015	4 Jul 2015 to 27 Dec 2015	Valid
	GW-RS0723-15	2 July 2015	7 Jul 2015 to 6 Jan 2015	Valid
GW-RS0831-15	31 July 2015	3 Aug 2015 to 28 Jan 2015	Valid	
Discharge Licence	WT00006757-2010	28 May 2010	31 May 2015	Expired
	WT00007129-2010	28 July 2010	31 Jul 2015	Valid
	WT00008982-2011	26 Apr 2011	30 April 2016	Valid

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
	WT00009691-2011	1 Aug 2011	31 July 2016	Valid
Billing Account under Waste Disposal Ordinance (Land)	7010255	10 Feb 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance (Marine)	7011496	6 Oct 2010	N/A	Valid
Registration as Chemical Waste Producer (Wan Chai)	WPN5213-135-C3 593-01	10 Mar 2010	N/A	Valid
Registration as Chemical Waste Producer (TKO 137)	WPN5213-839-C3 593-02	22 Sep 2010	N/A	Valid
Dumping Permit (Type 1 – Open Sea Disposal)	EP/MD/15-181	29 Dec 2014	1 Jan 2015 to 30 Jun 2015	Expired
	EP/MD/16-034	26 Jun 2015	1 Jul 2015 to 21 Dec 2015	Valid

**Table 3.5 Summary of submission status under FEP-03/356/2009 Condition**

EP Condition	Submission	Date of Submission
Condition 1.12	Commencement Date of Construction of Marine Works	8 April 2010
Condition 2.6	Management Organization of Main Construction Companies	10 April 2010
Condition 2.7	Works Schedule and Location Plans	8 April 2010
Condition 2.8	Silt Curtain Deployment Plan (Revision A)	20 April 2010
	Silt Curtain Deployment Plan (Revision B)	25 May 2010
	Silt Curtain Deployment Plan (Revision C)	14 Jun 2010
	Silt Curtain Deployment Plan (Revision H)	15 Feb 2011
	Silt Curtain Deployment Plan (Revision I)	17 Nov 2011
	Silt Curtain Deployment Plan (Revision J)	15 Feb 2012
	Silt Curtain Deployment Plan (Revision K)	3 May 2012
	Silt Curtain Deployment Plan (Revision L)	25 Oct 2012
	Silt Curtain Deployment Plan (Revision M)	30 Nov 2012
Condition 2.9	Silt Screen Deployment Plan	21 April 2010
	Supplementary Information for Existing WSD Salt Water Intakes at Quarry Bay and Sai Wan Ho	5 Oct 2010
	Silt Screen Deployment Plan (Revision B)	15 Feb 2012

EP Condition	Submission	Date of Submission
	Silt Screen Deployment Plan (Revision C)	3 May 2012
	Silt Screen Deployment Plan (Revision D)	10 Dec 2012
Condition 2.17	Noise Management Plan	6 May 2010
Condition 2.18	Landscape Plan (Decorative Screen Hoarding)	11 May 2010
	Landscape Plan (Control of Night Time Lighting)	2 June 2010
	Landscape Plan (Combined Version)	20 July 2011
	Landscape Plan (Combined Version)	5 Aug 2011
-----	Acknowledge of Submission	22 Aug 2011

Contract no. HY/2009/15 – Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

3.1.6. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HY/2009/15 under FEP-04/356/2009 are shown in **Table 3.6** and **Table 3.7**.

**Table 3.6 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/15**

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-04/356/2009	22 Nov 2010	N/A	Valid
Notification of Works Under APCO	321822	24 Sep 2010	N/A	Valid
Construction Noise Permit (CNP) for concreting works at Eastern Breakwater of CBTS	GW-RS0150-15	11 Feb 2015	13 Feb 2015 to 10 Aug 2015	Expired
Construction Noise Permit (CNP) for concreting works at Eastern Breakwater of CBTS	GW-RS0893-15	17 Aug 2015	17 Aug 2015 to 16 Feb 2016	Valid
Construction Noise Permit (CNP) for reclamation and d-wall works at Ex-PCWA	GW-RS0579-15	29 May 2015	31 May 2015 to 26 Nov 2015	Valid
Registration as a Chemical Waste Producer	WPN5213-147-C116 9-35	15 Nov 2010	N/A	Valid
Billing Account under Waste Disposal Ordinance	7011553	30 Sep 2010	27 Sep 2010 to 27 Jan 2016	Valid
Billing Account under Waste Disposal Ordinance (Disposal by Vessel)	7011761	26 Jun 2015	17 Jul 2015 to 16 Oct 2015	Valid

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Dumping Permit (Type 1 – Open Sea Disposal)	EP/MD/16-051	3 Aug 2015	5 Aug 2015 to 30 Jan 2016	Valid
Dumping Permit (Type 1 – Open Sea Disposal(Dedicated Site) and Type 2 – Confined Marine Disposal)	EP/MD/16-041	10 Jul 2015	15 Jul 2015 to 14 Aug 2015	Expired
	EP/MD/16-063	18 Aug 2015	20 Aug 2015 to 19 Sep 2015	Valid

**Table 3.7 Summary of submission status under FEP-04/356/2009 Condition**

FEP Condition	Submission	Date of Submission
Condition 2.6	Management Organization of Main Construction Companies	30 Sep 2010
	Amendment for Management Organization of Main Construction Companies	16 May 2011
Condition 2.7	Works Schedule and Location Plans	27 Oct 2010
	Amendment for Works Schedule and Location Plans	12 Nov 2010
Condition 2.8	Silt Curtain Deployment Plan	30 Nov 2010
	Amendment for Silt Curtain Deployment Plan	24 Feb 2011
	Amendment for Silt Curtain Deployment Plan	11 May 2011
	Amendment for Silt Curtain Deployment Plan	11 Sep 2012
	Amendment for Silt Curtain Deployment Plan	30 Oct 2012
Condition 2.9	Silt Screen Deployment Plan	19 Oct 2010
	Amendment for Silt Screen Deployment Plan	18 Feb 2011
	Amendment for Silt Screen Deployment Plan	15 Jun 2011
Condition 2.18	Proposal for the Removal of Odorous Sediment and Slime	13 Jan 2011
	Amendment for Proposal for the Removal of Odorous Sediment and Slime	8 Mar 2011
	Amendment for Proposal for the Removal of Odorous Sediment and Slime	2 Aug 2011
Condition 2.21	Landscape Plan	18 Feb 2011
Condition 2.23	Noise Management Plan	20 Oct 2010
	Amendment for Noise Management Plan	27 Jan 2011

3.1.7. Implementation status of the recommended mitigation measures during this reporting period is presented in **Appendix 3.1.**

Contract no. HY/2009/19 – Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

3.1.8. Summary of the current status on licences and/or permits on environmental protection pertinent for contract no. HY/2009/19 is shown in **Table 3.8**

**Table 3.8 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2009/19**

Permit / Licence / Notification / Approval	Reference No.	Issued Date	Valid Period / Expiry date	Status
Further Environmental Permit	FEP-07/364/2009/A	20 Sep 2012	Granted	Valid
Notification of Works Under APCO	326160	24 Jan 2011	Notified	Valid
Construction Noise Permit (CNP) (For Portion Vi Marine)	GW-RS0741-15	10 Jul 2015	23 Jul 2015 to 22 Jan 2016	Valid
	GW-RS0909-15	21 Aug 2015	21 Aug 2015 to 20 Feb 2016	Valid
Discharge License (Sea)	WT00010865-2011	03 Nov 2011	30-Nov-16	Valid
C&D Waste Disposal	7012306	10 Feb 2011	Registered	-
Vessel Disposal	7013285	21 July 2011	Registered	-
Registration as Chemical Waste Producer	5213-151-C3654-01	24 Mar 2011	Registered	-

Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

3.1.9. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HK/2012/08 under FEP-06/356/2009 are shown in **Table 3.9** and **Table 3.10**.

**Table 3.9 Cumulative Summary of Valid Licences and Permits under Contract no. HK/2012/08**

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-06/356/2009	5 Mar 2013	N/A	Valid
Notification of Works Under APCO	355439	4 Feb 2013	N/A	Valid
Registration as a Chemical Waste Producer	5213-134-C3790-01	8 Mar 2013	N/A	Valid
Billing Account under Waste Disposal Ordinance	7016883	18 Feb 2013	18 Jul 2017	Valid

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Water Discharge Licence	WT00018223-2014	28 Jan 2014	31 Jan 2019	Superseded by WT0002059 4-2014
	WT00020594-2014	22 Dec 2014	31 Jan 2019	Valid
Construction Noise Permit	GW-RS0295-15	19 Mar 2015	27 Mar 2015 to 26 Sep 2015	Valid
	GW-RS0296-15	19 Mar 2015	23 Mar 2015 to 22 Sep 2015	Valid
	PP-RS0008-15	10 Mar 2015	12 Mar 2015 to 11 Sep 2015	Valid
	GW-RS0145-15	11 Feb 2015	13 Feb 2015 to 12 Aug 2015	Expired
	GW-RS0144-15	12 Feb 2015	13 Feb 2015 to 12 Aug 2015	Expired
	GW-RS0223-15	3 Mar 2015	9 Mar 2015 to 8 Sep 2015	Valid
	GW-RS-0360-15	1 Apr 2015	2 May 2015 to 31 Oct 2015	Valid
	GW-RS0838-15	31 Jul 2015	3 Aug 2015 to 2 Feb 2016	Valid
	GW-RS0835-15	3 Aug 2015	5 Aug 2015 to 2 Feb 2016	Valid
Dumping Permit (Type 1 – Open Sea Disposal)	EP/MD/16-037	30 Jun 2015	2 Jul 2015 to 1 Jan 2016	Valid
Dumping Permit (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine disposal)	EP/MD/16-038	30 Jun 2015	2 Jul 2015 to 1 Aug 2015	Expired
	EP/MD/16-053	29 Jul 2015	2 Aug 2015 to 1 Sep 2015	Valid

**Table 3.10 Summary of submission status under EP-356/2009 and FEP-06/356/2009 Condition**

FEP Condition	Submission	Date of Submission
Condition 2.8	Silt Curtain Deployment Plan (Rev. 3)	Submitted on 25 Nov 2013 was returned to CSLJV by EPD.
Condition 2.9	Silt Screen Deployment Plan (Rev. 2)	Generally in order as commented by EPD on 19 Sep 2013
Condition 2.23	Noise Management Plan (Rev. 2)	Generally in order as commented by EPD on 15 Aug 2013
Condition 2.24	Landscape Plan (Rev. 3)	Generally in order as commented by EPD on 31 Oct 2013

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8)

3.1.10. Summary of the current status on licences and/or permits on environmental protection pertinent and submission for contract no. HY/2010/08 under FEP-07/356/2009 are shown in Table 3.11 and Table 3.12.

**Table 3.11 Cumulative Summary of Valid Licences and Permits under Contract no. HY/2010/08**

Permits and/or Licences	Reference No.	Issued Date	Valid Period/ Expiry Date	Status
Further Environmental Permit	FEP-07/356/2009	26 Jul 2013	NA	Valid
	FEP-10/364/2009/B	26 Jul 2013	NA	Valid
Notification of Works Under APCO	357176	2 Apr 2013	NIL	Valid
Registration as a Chemical Waste Producer	WPN5213-147-C11 69-44	27 Mar 2013	NIL	Valid
Billing Account under Waste Disposal Ordinance	7017170	27 Mar 2013	NIL	Valid
Billing Account under Waste Disposal Ordinance (Dumping by Vessel)	7020947	22 Dec 2014	NIL	Valid.
Water Discharge Licence	WT00020753-2015	3 Feb 2015	28 Feb 2017	Valid
Construction Noise Permit	GW-RS0154-15	11 Feb 2015	12 Feb 2015 to 8 Aug 2015	Expired
	GW-RS0309-15	20 Mar 2015	21 Mar 2015 to 19 Sep 2015	Valid
	GW-RS0531-15	18 May 2015	18 May 2015 to 17 Nov 2015	Valid
	GW-RS0811-15	24 Jul 2015	29 Jul 2015 to 28 Jan 2016	Valid
Dumping Permit (Type 1 – Open Sea Disposal)	EP/MD/15-169	9 Feb 2015	8 Aug 2015	Expired
	EP/MD/16-057	10 Aug 2015	12 Aug 2015 to 11 Feb 2016	Valid
Dumping Permit (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine disposal)	NIL	NIL	NIL	NIL

**Table 3.12 Summary of submission status under EP-356/2009 and FEP-07/356/2009 Condition**

FEP Condition	Submission	Date of Submission
Condition 2.8	Silt Curtain Deployment Plan (rev03)	24 Dec 2014
Condition 2.9	Silt Screen Deployment Plan (rev02)	18 Feb 2015



---

FEP Condition	Submission	Date of Submission
Condition 2.23	Noise Management Plan (rev02)	25 Mar 2014
Condition 2.24	Landscape Plant (rev04)	23 Sep 2014

## Monitoring Requirements

### 4.1 Noise Monitoring

#### NOISE MONITORING STATIONS

- 4.1.1. The noise monitoring stations for the Project are listed and shown in **Table 4.1** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

**Table 4.1 Noise Monitoring Station**

Station	Description
M1a	Harbour Road Sports Centre
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School

#### REAL-TIME NOISE MONITORING STATIONS

- 4.1.2. The real-time noise monitoring stations for the Project are listed and shown in **Table 4.2** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.
- 4.1.3. The real-time noise monitoring at RTN2-Oil Street Community Liaison Centre has been relocated to City Garden Electric Centre (RTN2a- Electric Centre) on 5 Oct 2012, which is a representative of noise sensitive receiver- City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted in Electric Centre from 4 December 2009 to 17 December 2009.
- 4.1.4. As the land-based piling and filling works- DP3 at Tin Hau had been completed on 3 September 2012 and confirmed by RSS, the real-time noise monitoring results at RTN1 - FEHD Hong Kong Transport Section Whitfield Depot was excluded under EP-356/2009 since 28 November 2012.

**Table 4.2 Real Time Noise Monitoring Station**

District	Station	Description
North Point	RTN2a	Electric Centre

- Real time noise monitoring results and graphical presentation during night time period are for information only.
- RTN2 had been relocated to RTN2a since 5 Oct 2012

#### NOISE MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.1.5. The construction noise level shall be measured in terms of the A-weighted equivalent continuous sound pressure level ( $L_{eq}$ ).  $L_{eq}$  (30 minutes) shall be used as the monitoring parameter for the time period between 0700 and 1900 hours on normal weekdays. For all other time periods,  $L_{eq}$  (5 minutes) shall be employed for comparison with the Noise Control Ordinance (NCO)

criteria. Supplementary information for data auditing, statistical results such as L10 and L90 shall also be obtained for reference.

4.1.6. Noise monitoring shall be carried out at all the designated monitoring stations. The monitoring frequency shall depend on the scale of the construction activities. The following is an initial guide on the regular monitoring frequency for each station on a weekly basis when noise generating activities are underway:

- One set of measurements between 0700 and 1900 hours on normal weekdays.

4.1.7. If construction works are extended to include works during the hours of 1900 – 0700 as well as public holidays and Sundays, additional weekly impact monitoring shall be carried out during respective restricted hours periods. Applicable permits under NCO shall be obtained by the Contractor.

**MONITORING EQUIPMENT**

4.1.8. As referred to in the Technical Memorandum <sup>TM</sup> issued under the NCO, sound level meters in compliance with the International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1) specifications shall be used for carrying out the noise monitoring. Immediately prior to and following each noise measurement the accuracy of the sound level meter shall be checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration level from before and after the noise measurement agree to within 1.0 dB.

4.1.9. Noise measurements shall not be made in fog, rain, wind with a steady speed exceeding 5 m/s or wind with gusts exceeding 10 m/s. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

**4.2 Air Monitoring**

**AIR QUALITY MONITORING STATIONS**

4.2.1. The air monitoring stations for the Project are listed and shown in **Table 4.3** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

**Table 4.3 Air Monitoring Station**

Station ID	Monitoring Location	Description
CMA1b	Oil Street Site Office**	North Point
CMA2a	Causeway Bay Community Centre	Causeway Bay
CMA3a	CWB PRE Site Office *	Causeway Bay
CMA4a	Society for the Prevention of Cruelty to Animals	Wan Chai
CMA5b	Pedestrian Plaza***	Wan Chai
CMA6a	WDII PRE Site Office *	Wan Chai

Remarks\*: As per the ENPC meeting in March 2011, the monitoring stations CMA3a – Future CWB site office at Wanchai Waterfront Promenade was renamed as remark.

Remarks\*\*: The location ID of monitoring station CMA1b was updated as “Oil Street Site Office” in April 2013.

Remarks\*\*\*: The station ID and monitoring location was updated in December 2014 with respect to monitoring station relocation.

#### AIR MONITORING PARAMETERS, FREQUENCY AND DURATION

- 4.2.2. One-hour and 24-hour TSP levels should be measured to indicate the impacts of construction dust on air quality. The 24-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B.
- 4.2.3. All relevant data including temperature, pressure, weather conditions, elapsed-time meter reading for the start and stop of the sampler, identification and weight of the filter paper, and any other local atmospheric factors affecting or affected by site conditions, etc., shall be recorded down in detail.
- 4.2.4. For regular impact monitoring, the sampling frequency of at least once in every six-days, shall be strictly observed at all the monitoring stations for 24-hour TSP monitoring. For 1-hour TSP monitoring, the sampling frequency of at least three times in every six-days should be undertaken when the highest dust impact occurs.

#### SAMPLING PROCEDURE AND MONITORING EQUIPMENT

- 4.2.5. High volume samplers (HVSs) in compliance with the following specifications shall be used for carrying out the 1-hour and 24-hour TSP monitoring:
- 0.6 – 1.7 m<sup>3</sup> per minute adjustable flow range;
  - equipped with a timing / control device with +/- 5 minutes accuracy for 24 hours operation;
  - installed with elapsed-time meter with +/- 2 minutes accuracy for 24 hours operation;
  - capable of providing a minimum exposed area of 406 cm<sup>2</sup>;
  - flow control accuracy: +/- 2.5% deviation over 24-hour sampling period;
  - equipped with a shelter to protect the filter and sampler;
  - incorporated with an electronic mass flow rate controller or other equivalent devices;
  - equipped with a flow recorder for continuous monitoring;
  - provided with a peaked roof inlet;
  - incorporated with a manometer;
  - able to hold and seal the filter paper to the sampler housing at horizontal position;
  - easily changeable filter; and
  - capable of operating continuously for a 24-hour period.
- 4.2.6. Initial calibration of dust monitoring equipment shall be conducted upon installation and thereafter at bi-monthly intervals. The transfer standard shall be traceable to the internationally recognized primary standard and be calibrated annually. The concern parties such as IEC shall properly document the calibration data for future reference. All the data should be converted into standard temperature and pressure condition.

#### LABORATORY MEASUREMENT / ANALYSIS

- 4.2.7. A clean laboratory with constant temperature and humidity control, and equipped with necessary measuring and conditioning instruments to handle the dust samples collected, shall be available for sample analysis, and equipment calibration and maintenance. The laboratory should be HOKLAS accredited.
- 4.2.8. An alternative non-HOKLAS accredited laboratory was set-up for carrying out the laboratory analysis, the laboratory equipment was approved by the ER on 8 February 2011 and the measurement procedures were witnessed by the IEC. Any measurement performed by the laboratory was demonstrated to the satisfaction of the ER and IEC. IEC shall regularly audit the measurement performed by the laboratory to ensure the accuracy of measurement results.
- 4.2.9. Filter paper of size 8" x 10" shall be labelled before sampling. It shall be a clean filter paper with no pinholes, and shall be conditioned in a humidity-controlled chamber for over 24-hours and be pre-weighed before use for the sampling.
- 4.2.10. After sampling, the filter paper loaded with dust shall be kept in a clean and tightly sealed plastic bag. The filter paper shall then be returned to the laboratory for reconditioning in the humidity controlled chamber followed by accurate weighing by an electronic balance with readout down to 0.1 mg. The balance shall be regularly calibrated against a traceable standard.
- 4.2.11. All the collected samples shall be kept in a good condition for 6 months before disposal.

#### IMPACT MONITORING FOR ODOUR PATROL

- 4.2.12. Odour patrols along the shorelines of Causeway Bay Typhoon Shelter and ex-Wan Chai Public Cargo Working Area when there is temporary reclamation in Causeway Bay Typhoon Shelter and/or in the ex-Wan Chai Public Cargo Working Area, or when there is dredging of the odorous sediment and slime at the south-western corner of the Causeway Bay Typhoon Shelter. Odour patrols will be carried out at bi-weekly intervals during July, August and September by a qualified person of the ET who shall:
- be at least 16 years of age;
  - be free from any respiratory illnesses; and
  - not be allowed to smoke, eat, drink (except water) or use chewing gum or sweets 30 min before and during odour patrol
- 4.2.13. Odour patrol shall be conducted by independent trained personnel / competent persons patrolling and sniffing around the shore as shown in **Figure 4.1** to detect any odour at the concerned hours (afternoon is preferred for higher daily temperature).
- 4.2.14. The qualified person will use the nose (olfactory sensor) to sniff odours at different locations. The main odour emission sources and the areas to be affected by the odour nuisance will be identified.
- 4.2.15. The perceived odour intensity is to be divided into 5 levels which are ranked in the descending order as follows:

- 0 – Not detected. No odour perceived or an odour so weak that it cannot be easily characterized or described;
- 1 – Slight Identifiable odour, and slight chance to have odour nuisance;
- 2 – Moderate Identifiable odour, and moderate chance to have odour nuisance;
- 3 – Strong Identifiable, likely to have odour nuisance;
- 4 – Extreme Severe odour, and unacceptable odour level.

4.2.16. The findings including odour intensity, odour nature and possible odour sources, and also the local wind speed and direction at each location will be recorded. In addition, some relevant meteorological and tidal data such as daily average temperature, and daily average humidity, on that surveyed day will be obtained from the Hong Kong Observatory Station for reference. The Action and Limit levels for odour patrol are shown in **Appendix 4.1**.

4.2.17. The qualified odour patrol member has individual n-butanol thresholds complied with the requirement of European Standard Method of Air Quality – Determination of Odour Concentration by Dynamic Olfactometry (EN13725) in the range of 20 to 80 ppb.

### 4.3 Water Quality Monitoring

4.3.1. The EIA Report has identified that the key water quality impact would be associated with the dredging works during the construction phase. Marine water quality monitoring for dissolved oxygen (DO), suspended solid (SS) and turbidity is therefore recommended to be carried out at selected WSD flushing water intakes. The impact monitoring should be carried out during the proposed dredging works to ensure the compliance with the water quality standards.

4.3.2. The updated EM&A Manual for EP-356/2009 (Version in March 2011) is approval by EPD on 29 April 2011. As such, the Action Level and Limit Level for the wet season (April – September) will be effected and applied to the water quality monitoring data from 30 April 2011.

#### Water Quality Monitoring Stations

4.3.3. It is proposed to monitor the water quality at 1 WSD salt water intakes and 7 cooling water intakes along the seafront of the Victoria Harbour. The proposed water quality monitoring stations of the Project are shown in **Table 4.4** and **Figure 4.1**. **Appendix 4.1** shows the established Action/Limit Levels for the monitoring works.

**Table 4.4 Marine Water Quality Stations for Water Quality Monitoring**

Station Ref.	Location	Easting	Northing
<b>WSD Salt Water Intake</b>			
WSD19	Sheung Wan	833415.0	816771.0
<b>Cooling Water Intake</b>			
C1	HKCEC Extension	835885.6	816223.0
C7	Windsor House	837193.7	816150.0
P1	HKCEC Phase I	835774.7	816179.4
P3	The Academy of performing Arts	835824.6	816212.0
P4	Shui on Centre	835865.6	816220.0

Station Ref.	Location	Easting	Northing
P5	Government Buildings (Wanchai Tower / Revenue Tower / Immigration Tower)	835895.2	816215.2
<b>Cooling Water Intake / WSD Salt Water Intake</b>			
RW21-P789	Great Eagle Centre/ Sun Hung Kai Centre/ WSD Wanchai salt water intake	836268.0	816020.0

WATER QUALITY PARAMETERS

- 4.3.4. Monitoring of dissolved oxygen (DO), turbidity and suspended solids (SS) shall be carried out at WSD flushing water intakes and cooling water intakes. DO and Turbidity are measured in-situ while SS is determined in laboratory.
- 4.3.5. In association with the water quality parameters, other relevant data shall also be measured, such as monitoring location/position, time, sampling depth, water temperature, pH, salinity, dissolved oxygen (DO) saturation, weather conditions, sea conditions, tidal stage, and any special phenomena and work underway at the construction site etc.

SAMPLING PROCEDURES AND MONITORING EQUIPMENT

- 4.3.6. The interval between two sets of monitoring should not be less than 36 hours except where there are exceedances of Action and/or Limit Levels, in which case the monitoring frequency will be increased. **Table 4.5** shows the proposed monitoring frequency and water quality parameters. Duplicate in-situ measurements and water sampling should be carried out in each sampling event. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.

**Table 4.5 Marine Water Quality Monitoring Frequency and Parameters**

Activities	Monitoring Frequency <sup>1</sup>	Parameters <sup>2</sup>
During the 4-week baseline monitoring period	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
During marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity
After completion of marine construction works	Three days per week, at mid-flood and mid-ebb tides	Turbidity, Suspended Solids (SS), Dissolved Oxygen (DO), pH, Temperature, Salinity

Notes:

- 1. For selection of tides for in-situ measurement and water sampling, tidal range of individual flood and ebb tides should be not less than 0.5m.
- 2. Turbidity should be measured in situ whereas SS should be determined by laboratory.

#### DISSOLVED OXYGEN AND TEMPERATURE MEASURING EQUIPMENT

- 4.3.7. The instrument should be a portable, weatherproof dissolved oxygen measuring instrument complete with cable, sensor, comprehensive operation manuals, and use a DC power source. It should be capable of measuring:
- a dissolved oxygen level in the range of 0-20 mg/l and 0-200% saturation
  - a temperature of 0-45 degree Celsius
- 4.3.8. It should have a membrane electrode with automatic temperature compensation complete with a cable. Sufficient stocks of spare electrodes and cables should be available for replacement where necessary. (e.g. YSI model 59 meter, YSI 5739 probe, YSI 5795A submersible stirrer with reel and cable or an approved similar instrument).
- 4.3.9. Should salinity compensation not be build-in in the DO equipment, in-situ salinity shall be measured to calibrate the DO equipment prior to each DO measurement.

#### TURBIDITY MEASUREMENT INSTRUMENT

- 4.3.10. The instrument should be a portable, weatherproof turbidity-measuring instrument complete with comprehensive operation manual. The equipment should use a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0-1000 NTU and be complete with a cable (e.g. Hach model 2100P or an approved similar instrument).

#### SAMPLER

- 4.3.11. A water sampler comprises a transparent PVC cylinder, with a capacity of not less than 2 litres, and can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth (e.g. Kahlsico Water Sampler or an approved similar instrument).

#### SAMPLE CONTAINER AND STORAGE

- 4.3.12. Water samples for suspended solids measurement should be collected in high-density polythene bottles, packed in ice (cooled to 4°C without being frozen), and delivered to ALS Technichem (HK) Pty Ltd. as soon as possible after collection for analysis.

#### WATER DEPTH DETECTOR

- 4.3.13. A portable, battery-operated echo sounder shall be used for the determination of water depth at each designated monitoring station. This unit can either be handheld or affixed to the bottom of the workboat, if the same vessel is to be used throughout the monitoring programme.

#### SALINITY

- 4.3.14. A portable salinometer capable of measuring salinity in the range of 0-40 ppt shall be provided for measuring salinity of the water at each of monitoring location.

#### MONITORING POSITION EQUIPMENT

- 4.3.15. A hand-held or boat-fixed type digital Global Positioning System (GPS) with waypoint bearing indication or other equivalent instrument of similar accuracy shall be provided and used during

monitoring to ensure the monitoring vessel is at the correct location before taking measurements.

CALIBRATION OF IN-SITU INSTRUMENTS

- 4.3.16. All in-situ monitoring instrument shall be checked, calibrated and certified by a laboratory accredited under HOKLAS or equivalent before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the water quality monitoring. Responses of sensors and electrodes should be checked with certified standard solutions before each use. Wet bulb calibration for a DO meter shall be carried out before measurement at each monitoring location.
- 4.3.17. For the on site calibration of field equipment by the ET, the BS 127:1993, "Guide to Field and on-site test methods for the analysis of waters" should be observed.
- 4.3.18. Sufficient stocks of spare parts should be maintained for replacements when necessary. Backup monitoring equipment shall also be made available so that monitoring can proceed uninterrupted even when some equipment is under maintenance, calibration, etc.
- 4.3.19. Current calibration certificates of equipments are presented in [Appendix 4.2](#).

LABORATORY MEASUREMENT / ANALYSIS

- 4.3.20. Analysis of suspended solids has been carried out in a HOKLAS accredited laboratory, ALS Technichem (HK) Pty Ltd. Water samples of about 1L shall be collected at the monitoring stations for carrying out the laboratory SS determination. The SS determination work shall start within 24 hours after collection of the water samples. The SS determination shall follow APHA 19ed or equivalent methods subject to the approval of IEC and EPD.

ENHANCED WATER QUALITY MONITORING IN THE EX-WAN CHAI PUBLIC CARGO WORKING AREA AND THE CAUSEWAY BAY TYPHOON SHELTER

- 4.3.21. The enhanced water quality monitoring and audit programme is to avoid aggravation of odour nuisance from seawater arising from temporary reclamation in the ex-Wan Chai Public Cargo Working Area and the Causeway Bay Typhoon Shelter.
- 4.3.22. Dissolved oxygen monitoring at the intakes C6 and C7 in Causeway Bay Typhoon Shelter when there is temporary reclamation in Causeway Bay Typhoon Shelter and at the south-western and south-eastern corners of the ex-Wan Chai Public Cargo Working Area. The proposed water quality monitoring stations of the Project are shown in **Table 4.6** and [Figure 4.1](#).

**Table 4.6 Marine Water Quality Stations for Enhanced Water Quality Monitoring**

Station	Location
C6	Excelsior Hotel
C7	Windsor House
Ex-WPCWA-SW	South-western of the ex-Wan Chai Public Cargo Working Area
Ex-WPCWA-SE	South-eastern of the ex-Wan Chai Public Cargo Working Area

- Water quality monitoring for Windsor House Cooling (Station Ref: C7) was temporarily suspended since 22 October 2014 with respect to the diversion scheme.

- Enhanced DO monitoring stations (Ex-PCWA SW and Ex-PCWA SE) was finely adjusted to the PCWAE since 7 November 2014.
- 4.3.23. The monitoring of dissolved oxygen are to be carried out 3 days per week, at mid-flood and mid-ebb tides for 3 water depths (1m below water surface, mid-depth and 1m above sea bed, except where the water depth less than 6m, the mid-depth may be omitted. If the water depth be equal to or less than 3m, only the mid-depth will be monitored).

#### DAILY SS MONITORING AND 24 HOURS TURBIDITY MONITORING SYSTEM

- 4.3.24. During dredging of the sediment at the south-western corner of the Causeway Bay Typhoon Shelter, daily monitoring of suspended solids and 24 hour monitoring of turbidity at the cooling water intakes (C6 and C7) shall be conducted.
- 4.3.25. The 24 hours monitoring of turbidity at the cooling water intakes (C6 and C7) shall be established by setting up a continuous water quality monitoring station in front of the intakes during the dredging activities. The monitoring system include the turbidity sensor and data logger which is capable of data capturing at every 5 minutes. The data shall be downloaded daily and compared with the Action and Limit level determined during the baseline water quality monitoring at the cooling water intake locations.

#### ADDITIONAL DISSOLVED OXYGEN MONITORING FOR CULVERT L WATER DISCHARGE FLOW

- 4.3.26. In response to the Condition 2.18 of the Environmental Permit no. EP-356/2009 requiring that a silt curtain / impermeable barrier system be installed to channel water discharge flow from Culvert L to locations outside the embayment area, a proposed replacement of the requirement with additional dissolved oxygen monitoring has been conducted at three monitoring stations, namely A, B and C between the eastern seawall of Central Reclamation Phase III and the HKCEC Extension since November 2011 under EP-356/2009 so that DO level between the eastern seawall of Central Reclamation Phase II and the HKCEC extension could be continuously monitored.
- 4.3.27. With respect to the commencement of dredging works under HK/2012/08 and the installation of MTR precast protection unit, the enhanced water quality monitoring for Culvert L was temporarily suspended since 24 July 2013
- 4.3.28. The monitoring of dissolved oxygen are to be carried out once per week, at mid-flood and mid-ebb tides for 3 water depths (1m below water surface, mid-depth and 1m above sea bed, except where the water depth less than 6m, the mid-depth may be omitted. If the water depth be equal to or less than 3m, only the mid-depth will be monitored).

**5. Monitoring Results**

5.0.1. The environmental monitoring will be implemented based on the division of works areas of each designed project managed under different contracts with separate FEP applied by individual contractors. Overall layout showing work areas of various contracts, latest status of work commencement and monitoring stations is shown in **Figure 2.1** and **Figure 4.1**. The monitoring results are presented in according to the Individual Contract(s).

5.0.2. In the reporting month, the concurrent contracts are as follows:

- Contract no. HK/2009/01 – Wan Chai Development Phase II – Central-Wan Chai Bypass at Hong Kong Convention and Exhibition Centre; and
- Contract no. HK/2009/02 Wan Chai Development Phase II – Central-Wan Chai Bypass at Wan Chai East
- Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)
- Contract no. HY/2009/19- Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link
- Contract no. HK/2012/08 – Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West
- Contract no. HY/2010/08 – Central- Wanchai Bypass Tunnel (Slip Road 8 Section)

5.0.3. The environment monitoring schedules for reporting month and coming month are presented in **Appendix 5.1**.

**5.1 Noise Monitoring Results**

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC, Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

5.1.1. The proposed division of noise monitoring stations are summarized in **Table 5.1** below.

**Table 5.1 Noise Monitoring Station for Contract nos. HK/2009/01 and HK/2009/02**

Station	Description
M1a	Harbour Road Sports Centre

5.1.2. No action or limit level exceedance was recorded in this reporting month.

5.1.3. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 5.2**.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

5.1.4. The noise monitoring for HY/2009/15 was commenced on 10 November 2010. The proposed division of noise monitoring stations are summarized in **Table 5.2** below.

**Table 5.2 Noise Monitoring Station for Contract no. HY/2009/15**

Station	Description
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station

5.1.5. No action or limit level exceedance was recorded in this reporting month.

5.1.6. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 5.2**.

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

5.1.7. The proposed division of noise monitoring stations are summarized in **Table 5.3** below.

**Table 5.3 Noise Monitoring Station for Contract no. HY/2009/19**

Station	Description
M4b	Victoria Centre
M5b	City Garden
M6	HK Baptist Church Henrietta Secondary School

5.1.8. No action or limit level exceedance was recorded in this reporting month.

5.1.9. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 5.2**.

Contract no. HY/2010/08-Central-Wanchi Bypass Tunnel (Slip Road 8 Section)

5.1.10. The proposed division of noise monitoring stations are summarized in **Table 5.4** below.

**Table 5.4 Noise Monitoring Station for Contract no. HY/2010/08**

Station	Description
M2b	Noon Gun Area
M3a	Tung Lo Wan Fire Station

- 5.1.11. No action or limit level exceedance was recorded in this reporting month.
- 5.1.12. Noise monitoring results measured in this reporting period are reviewed and summarized. Details of noise monitoring results and graphical presentation can be referred in **Appendix 5.2**.

## 5.2 Real-time Noise Monitoring

### Contract no. HY/2009/19 – Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 5.2.1 As the marine-based piling and filling works- DP3 at Tin Hau had been completed on 3 September 2012 and confirmed by RSS, the real-time noise monitoring results at FEHD Hong Kong Transport Section Whitfield Depot was excluded under EP-356/2009 since 28 November 2012.
- 5.2.2 The real-time noise monitoring at RTN2-Oil Street Community Liaison Centre has been relocated to City Garden Electric Centre (RTN2a- Electric Centre) on 5 Oct 2012, which is a representative of noise sensitive receiver- City Garden. The baseline noise level of RTN2a will adopt the results derived from the baseline noise monitoring conducted in Electric Centre from 4 December 2009 to 17 December 2009.
- 5.2.3 The major work activities for Contract no. HY/2009/11 was confirmed substantial complete by RSS on 4 January 2012. The construction site was handed over to contractor HY/2009/19 on 31 December 2011 and the FEP-01/356/2009 was surrendered on 22 Oct 2012.
- 5.2.4 Real-time noise monitoring at FEHD Hong Kong Transport Section Whitfield Depot commenced external wall renovation since 1 June 2012

**Table 5.5 Real Time Noise Monitoring Station for Contract no. HY/2009/19**

District	Station	Description
North Point	RTN2a	Electric Centre

- *Real time noise monitoring results and graphical presentation during night time period are for information only.*
- *RTN2 had been relocated to RTN2a since 5 Oct 2012*
- *RTN1 monitoring had been finished on 28 Nov 2012*

- 5.2.5 **No limit level exceedance was recorded in this reporting month.**

5.2.6 Details of real time noise monitoring results and graphical presentation can be referred to [Appendix 5.5](#).

### 5.3 Air Monitoring Results

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

5.3.1. Air monitoring was commenced on 1 April 2011 in response to the commencement of the land-filling work for Contract no. HK/2009/01. The proposed divisions of air monitoring stations are summarized in **Table 5.6** below.

**Table 5.6 Air Monitoring Stations for Contract no. HK/2009/01**

Station	Description
CMA5b	Pedestrian Plaza
CMA6a	WDII PRE Site Office

5.3.2. No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in [Appendix 5.3](#).

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

5.3.3. Air monitoring was commenced in mid-January 2011 for the land-filling work for Contract no. HK/2009/02. The proposed division of air monitoring stations are summarized in **Table 5.7** below. No exceedance was recorded in the reporting month.

**Table 5.7 Air Monitoring Station for Contract no. HK/2009/02**

Station	Description
CMA4a	Society for the Prevention of Cruelty to Animals

5.3.4. No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in [Appendix 5.3](#).

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

5.3.5. Air monitoring was commenced on 15 March 2011 for the land filling work for Contract no. HY/2009/15. The proposed division of air monitoring stations are summarized in **Table 5.8** below.

**Table 5.8 Air Monitoring Station for Contract no. HY/2009/15**

Station	Description
CMA3a	CWB PRE Site Office

- 5.3.6. No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in **Appendix 5.3**.
- 5.3.7. The odour patrol along the odour route with 7 sniffing locations was conducted by a qualified odour patrol member on 4 and 18 August 2015 at the concerned hours (afternoon for higher daily temperature). No Action and Limit Level was recorded during this reporting month. The details of the odour patrol results and meteorological conditions and on the date of odour patrol are shown in **Appendix 5.3**.

Contract no. HY/2009/19- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 5.3.8. The proposed division of air monitoring stations are summarized in **Table 5.9** below.

**Table 5.9 Air Monitoring Stations for Contract no. HY/2009/19**

Station	Description
CMA1b	Oil Street Site Office
CMA2a	Causeway Bay Community Centre

- 5.3.9. One action level exceedance was recorded at monitoring station CMA2a on 26 August 2015 during 24hr TSP monitoring in the reporting month.
- 5.3.10. After investigation, it was found that external renovation at Causeway Bay Community Centre by non-CWB Contractor was the major contribution to air quality impact and no construction works with considerable dust impact was undertaken by the Contractor on the monitoring date. As such, the exceedance was considered as non-Project related.
- 5.3.11. Two action level exceedances were recorded at monitoring station CMA1a on 27 August 2015 during 1hr TSP monitoring in the reporting month.
- 5.3.12. After investigation, it was found that external renovation at Causeway Bay Community Centre by non-CWB Contractor was the major contribution to air quality impact and no construction works with considerable dust impact was undertaken by the Contractor on the monitoring date. As such, the exceedance was considered as non-Project related.
- 5.3.13. No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in **Appendix 5.3**.

Contract no. HK/2012/08- Wan Chai Development Phase II – Central-Wan Chai Bypass at Wan Chai West

- 5.3.14. The proposed division of air monitoring stations are summarized in **Table 5.10** below.

**Table 5.10 Air Monitoring Stations for Contract no. HK/2012/08**

Station	Description
CMA5b	Pedestrian Plaza

5.3.15. No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in **Appendix 5.3**.

Contract no. HY/2010/08- Central-Wanchai Bypass Tunnel (Slip Road 8 Section)

5.3.16. The proposed division of air monitoring stations are summarized in **Table 5.11** below. No exceedance was recorded in the reporting month.

**Table 5.11 Air Monitoring Stations for Contract no. HY/2010/08**

Station	Description
CMA3a	CWB PRE Site Office

5.3.17. No exceedance was recorded in the reporting month. Air quality monitoring results measured in this reporting period are reviewed and summarized. Details of air monitoring results and graphical presentation can be referred in **Appendix 5.3**.

**5.4 Water Monitoring Results.**

- 5.4.1. [Action and Limit level of water quality monitoring was transited from dry season to wet season from 1 April 2015.](#)
- 5.4.2. [With respect to the construction stage and access condition at Ex-PCWAW and the potential DO concern within the area, the suspended Enhance DO monitoring within Ex-PCWAW area at the Enhance DO monitoring station Ex-PCWA-SE was resumed on 10 August 2015 at the finely adjusted monitoring location.](#)
- 5.4.3. With respect to the commencement of seawall modification works at Ex-PCWAE and the location of the Enhance DO monitoring stations would form an active construction area, the Enhance DO monitoring at monitoring station EX-PCWA SW and SE were temporarily suspended from 2 March 2015 ebb tide and the monitoring at the location is tentatively to be resumed by early April 2015 to cater for the potential DO concern during Wet Season.
- 5.4.4. As informed by CWB RSS, the operation of the diverted Windsor House cooling intake was commenced on 20 Dec 2014 and the water quality monitoring at monitoring station C7 for Windsor House Cooling water intake was resumed on 22 Dec 2014
- 5.4.5. With respect to the commencement of temporary reclamation works and seawall construction at Ex-PCWAW zone and diverted culvert extension, the location of the Enhance DO monitoring stations (Ex-PCWASW and Ex-PCWA SE) were finely adjusted to the PCWAE since 7 November 2014.

- 5.4.6. With respect to the commencement of marine dredging works at WCR3 under contract HK/2009/02. The respective water quality monitoring station C1 were associated with HK/2009/01 and HK/2009/02.
- 5.4.7. As confirmed by CWB RSS, the operation of the pump station for Windsor House Cooling Water was suspended from 22 Oct 2014 for the Windsor House intake cooling intake scheme and temporary supply of freshwater from WSD water mains was provided to cooling water intake. The water quality monitoring for the respective cooling water intake at WQM station C7 was temporarily suspended from 22 Oct 2014.
- 5.4.8. With respect to the commencement of filling works at TS3 and the formation of TZ3 reclamation zone, the enhance DO monitoring at Enhance monitoring station C7 was temporarily suspended from 22 Oct 2014.
- 5.4.9. As confirmed by WDII RSS and IEC, the cross harbour dredging works have completed since 16 March 2012 while the dredging works for submarine outfall pipeline has completed since 29 November 2011, considering current construction stage and dredging Scenario, the water quality monitoring at stations WSD9 and WSD17 was temporarily suspended since 8 September 2014 flood tide.
- 5.4.10. With respect to the switching over of cooling water intake location, the water quality monitoring at the relocated intake station RW21-P789 under HK/2009/02 was commenced since 29 July 2013 and monitoring station C5e and C5w were temporarily suspended and switched over to monitoring station RW21-P789 on 29 July 2013 due to suspension of pump house operation.
- 5.4.11. As advised by WDII RSS, the water quality monitoring for WSD21 pump station with respect to HK/2009/02 was switched over to the relocated location since 12 March 2014. According to the EM&A Manual, the water quality monitoring station WSD21 was relocated to station RW21-P789 and the water quality monitoring at station WSD21 was temporarily suspended since 12 March 2014.
- 5.4.12. With respect to the commencement of marine dredging works under contract HY/2010/08. The respective water quality monitoring station C7 were associated with HY/2009/15 and HY/2010/08.
- 5.4.13. With respect to the commencement of marine dredging works under contract HK/2012/08/ The respective water quality monitoring station WSD19, P1, P3, P4, and P5 were associated with Contract HK/2012/08 Since September 2013.
- 5.4.14. WQM events on 22 April 2013 at monitoring stations C2, C3, C4e and C4w were temporarily suspended. Upon confirmation with WDII RSS and the IEC, water quality monitoring at relocated intakes monitoring location P1, P3, P4 and P5 were commenced since 24 April 2013.
- 5.4.15. Due to the marine piling under Contract no. HY/2009/19 was completed on 4 March 2013, the temporary suspension of impact water quality monitoring at C8 and C9 from 4 March 2013 have been monitored for 4-week period after the completion of marine works to confirm no water deterioration.

- 5.4.16. As confirmed by CWB RSS, the marine piling works under contract HY/2009/19 was confirmed completed by 4 March 2013. The water quality monitoring at the respective monitoring stations C8 and C9 were temporarily suspended since 30 March 2013.
- 5.4.17. RSS confirmed that all Type III Dredging works under HK/2009/01 have been completed since Oct 2012.
- 5.4.18. Due to the presence of obstacle within the inner silt curtain frame at sampling point, water quality point at C7 was finely adjusted to the outside of the inner silt curtain frame since 29 Dec 2012.
- 5.4.19. With respect to the trial dredging at WCR2 was scheduled on 20, 22, 24, 25 March and 1, 3, 11, 13, 15, 17, 19, 20 Apr and 3 May 2012, on-going water quality monitoring results at WSD21 during this period was checked and indicated that there was no contribution due to the trial dredging operation. Enhanced review of water quality around WCR2 was also implemented and no deterioration in the water quality was observed.
- 5.4.20. Due to the access of water monitoring station at WSD19 was blocked by LCSD construction works from 3 April 2012 to 2 May 2012 and lead to the inaccessibility of sampling either land and marine, there is a fine adjustment of the sampling point of WSD 19 since 5 April 2012 to the closest accessible point prior to the completion of the construction activities.
- 5.4.21. WDII/RSS advised that the dredging works for submarine pipeline at Victoria Harbour had been completed in January 2012. Therefore, the concurrent dredging activities at Sewage Pipeline Zone and reclamation shoreline zone TCBR under the EP-356/2009 scenario 2B no longer exist. As such, with reference to Table 5.39 of the EIA Report for Wan Chai Development Phase II and Central-Wan Chai Bypass, the application of silt screen for cooling water intakes for Queensway Government Offices was suspended and the others remain unchanged.
- 5.4.22. Due to the dredging works for Cross Harbour Water Mains from Wan Chai to Tsim Sha Tsui-DP6 was completed on 26 March 2012, the temporary suspension of impact water quality monitoring at WSD7 and WSD20 after 27 April 2012 for the water quality monitoring at WSD7 and WSD20 have been monitored for 4-week period after the completion of DP6 to confirm no water deterioration. Water quality monitoring at WSD10 and WSD15 was temporary suspended while water quality monitoring at WSD9 and WSD17 was implemented with respect to HK/2009/02 from 8 Feb 12 onwards;
- 5.4.23. Based on the joint inspection on 4 Jan 2012 for the NPR area, the 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8, C9 to confirm no water deterioration with respect to NPR was commenced since 7 Jan 2012 and it was completed on 6 February 2012.
- 5.4.24. Based on the safety concern when external façade refurbishment was conducted by contractor employed by Provident Centre (C9) between 9 January 2012 to 30 July 2012 which caused to the inaccessibility of sampling either land and marine since 3 Feb 2012, there is a fine adjustment of the sampling location of water quality monitoring at C9 since 10 March 2012 to the closest accessible point prior to the completion of the external façade refurbishment work.
- 5.4.25. Water quality monitoring at C8 and C9 have been implemented with respect to HY/2009/19 since the marine bore piling work started on 28 Jan 12.

**Table 5.12 Water Monitoring Stations for contracts with respect to remaining DP3 work areas after the completion of DP5 & DP6 in 2012 and intake diversion in 2013**

Contract No.	Remaining DP3 and work area(s)	Relevant Water Monitoring Stations,	Division of WQM w.r.t tentative works commenced / to be commenced
HK/2009/01	WCR3	C1 <sup>1</sup>	Apr 2013
HK/2009/02	WCR3, WCR4, TWCR4	RW21-P789 <sup>1</sup> , C1 <sup>1</sup>	Apr 2013
HK/2012/08	HKCEC2W, HKCEC2E	WSD19, P1 <sup>3</sup> , P3 <sup>3</sup> , P4 <sup>3</sup> , P5 <sup>3</sup>	Aug 2013
HY/2009/15	TCBR2, TCBR3, TCBR1W, TPCWAE, TPCWAW	C6 <sup>4</sup> , C7, Ex-WPCWA SW, Ex-WPCWA SE (plus enhanced DO monitoring)	Nov 2010
HY/2010/08	TCBR3, TCBR4	C6 <sup>4</sup> , C7 (plus enhanced DO monitoring)	Mar 2014

Remarks:

- The water monitoring stations for WSD19, P1, P3, P4, P5 shall be associated with Contract No. HK/2009/01 prior to their transition to Contract HK/2012/08.
- 4 intakes (re-provisioned Wanchai WSD intake, Great Eagle Centre, China Resources Centre & Sun Hung Kai Centre constructed adjacent to each other) taken as a single group for silt screen protection and monitoring.
- Re-provisioned intake reference: P1: HKCEC Phase 1; P3: APA, P4: Shui On; P5: Government Buildings (Wanchai Tower / Revenue Tower / Immigration Tower)
- Enhanced DO Monitoring at C6 since the intake abandon in May 2011.
- The water monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

5.4.26. Water monitoring for Contract no. HK/2009/01 was commenced on 23 July 2010. The proposed division of water monitoring stations are summarized in **Table 5.13** below.

**Table 5.13 Water Monitoring Stations for Contract no. HK/2009/01**

Station Ref.	Location	Easting	Northing
<b>Cooling Water Intake</b>			
C1	HKCEC Extension	835885.6	816223.0

Remarks:

- The water monitoring stations for the dredging works under Contract No. HK/2009/01 should also include WSD9, WSD17, WSD 21 and C5 if water quality monitoring at these locations have not been carried out by others. Similarly, the water monitoring stations for the dredging works under Contract No. HK/2009/02 should also include WSD7, WSD9, WSD17, WSD 19, C1, C2, C3 and C4 if water quality monitoring at these locations have not been carried out by others.
- WSD7 and WSD20 water quality monitoring were temporarily suspended since 27 Apr 2012.
- C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since 24 Apr 2013

Contract no. HK/2009/02 - Wan Chai Development Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

5.4.27. Water monitoring for Contract no. HK/2009/02 was commenced on 8 July 2010. The proposed division of water monitoring stations are summarized in **Table 5.14** below.

**Table 5.14 Water Monitoring Stations for Contract no. HK/2009/02**

Station Ref.	Location	Easting	Northing
<b>Cooling Water Intake</b>			
C1	HKCEC Extension	835885.6	816223.0
<b>Cooling Water Intake / WSD Salt Water Intake</b>			
RW21-P789	Great Eagle Centre/ Sun Hung Kai Centre/WSD Wanchai salt water intake	836268.0	816020.0

Remarks:

- The water monitoring stations for the dredging works under Contract No. HK/2009/01 should also include WSD9, WSD17, WSD 21 and C5 if water quality monitoring at these locations have not been carried out by others. Similarly, the water monitoring stations for the dredging works under Contract No. HK/2009/02 should also include WSD7, WSD9, WSD17, WSD 19, C1, C2, C3 and C4 if water quality monitoring at these locations has not been carried out by others.
- Water quality monitoring at WSD9 and WSD 17 was implemented with respect to HK/2009/02 from 8 Feb 2012.
- C5e and C5w water quality monitoring station was temporarily suspended since 29 July 2013
- WSD21 water quality monitoring station was temporarily suspended since 12 March 2014
- WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 September 2014 flood tide.
- The water monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area.

Contract no. HK/2012/08 - Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

5.4.28. Water monitoring for Contract no. HK/2012/08 was commenced on 5 March 2013. The proposed division of water monitoring stations are summarized in **Table 5.15** below.

**Table 5.15 Water Monitoring Stations for Contract no. HK/2012/08**

Station Ref.	Location	Easting	Northing
<b>WSD Salt Water Intake</b>			
WSD19	Sheung Wan	833415.0	816771.0
<b>Cooling Water Intake</b>			
P1	HKCEC Phase I	835774.7	816179.4
P3	The Academy of performing Arts	835824.6	816212.0
P4	Shui on Centre	835865.6	816220.0
P5	Government Buildings (Wanchai Tower / Revenue Tower / Immigration Tower)	835895.2	816215.2

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

- 5.4.29. As the removal of reclamation work of TS1 at CBTS has been completed, all procedures have been rectified and complied with the conditions set in EP-356/2009 and FEP-04/356/2009.
- 5.4.30. Due to the commencement of the maintenance dredging on 10 November 2010, water quality monitoring for Contract no. HY/2009/15 was commenced on 9 November 2010. The proposed division of water monitoring stations are summarized in Table 5.16 below.
- 5.4.31. Due to the presence of obstacle within the inner silt curtain frame at sampling point, water quality point at C7 was finely adjusted to the outside of the inner silt curtain frame since 29 Dec 2012.

**Table 5.16 Water Monitoring Stations for Contract no. HY/2009/15**

Station Ref.	Location	Easting	Northing
<b>Cooling Water Intake</b>			
C7	Windsor House	837193.7	816150.0

Remarks:

- The cessation of seawater intake operation for C6 was confirmed on 17 May 2011, the water monitoring at C6 was then terminated since 17 May 2011.
- Water quality monitoring for Windsor House Cooling (Station Ref: C7) was temporarily suspended since 22 October 2014 with respect to the diversion scheme and was resumed since 22 December 2014.

Contract no. HY/2009/19 – Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 5.4.32. Due to the commencement of the marine bored piling on 28 Jan 2012, water quality monitoring for Contract no. HY/2009/19 was commenced on 28 Jan 2012.
- 5.4.33. Due to the marine piling under Contract no. HY/2009/19 was completed on 4 March 2013, the temporary suspension of impact water quality monitoring at C8 and C9 from 4 March 2013 have been monitored for 4-week period after the completion of marine works to confirm no water deterioration.
- 5.4.34. Based on the safety concern when external façade refurbishment was conducted by contractor employed by Provident Center (C9) between 9 January 2012 to 30 July 2012 which caused to the inaccessibility of sampling either land and marine since 3 Feb 2012, there is a fine adjustment of the sampling location of water quality monitoring at C9 since 10 March 2012 to the closest accessible point prior to the completion of the external façade refurbishment work.
- 5.4.35. Due to the access of water monitoring station at WSD19 was blocked by LCSD construction works from 3 April 2012 to 2 May 2012 and lead to the inaccessibility of sampling either land and marine, there is a fine adjustment of the sampling point of WSD 19 since 5 April 2012 to the closest accessible point prior to the completion of the construction activities.

- 5.4.36. As per the meeting with the representative of Excelsior Hotel and World Trade Centre on 17 May 2011, they confirmed that the seawater intake for The Excelsior was no longer in use and replaced by the connected permanent water supply from WSD pipelines since 11 January 2011. Thus, the impact water quality monitoring for the cooling intake - C6 was terminated effective from 26 May 2011.
- 5.4.37. 24 hours monitoring of turbidity at the cooling water intakes at C7 was conducted. With respect to the seawall collapsing at TS4 on 17 November 2011, the 24 hours turbidity monitoring and was kept in November 2011. Since the reinstating the seawall was completed on 13 January 2012 and no any water deterioration was performed, 24 hour turbidity monitoring was then suspended on 27 January 2012.
- 5.4.38. Water monitoring results measured in this reporting period are reviewed and summarized. Details of water quality monitoring results and graphical presentation can be referred in **Appendix 5.4**.

**Table 5.17 Summary of Water Quality Monitoring Exceedances in Reporting Month**

Contract no.	Water Monitoring Station	Mid-flood						Mid-ebb					
		DO		Turbidity		SS		DO		Turbidity		SS	
		AL	LL	AL	LL	AL	LL	AL	LL	AL	LL	AL	LL
HK/2009/01 & HK/2009/02	C1	0	0	0	0	0	0	0	0	0	0	0	0
HK/2012/08	WSD19	0	0	0	0	0	0	0	0	0	0	0	0
	P1	0	0	0	0	0	0	0	0	0	0	0	0
	P3	0	0	0	0	0	0	0	0	0	0	0	0
	P4	0	0	0	0	0	0	0	0	0	0	0	0
	P5	0	0	0	0	0	0	0	0	0	0	0	0
HK/2009/02	RW21-P789	0	0	0	0	0	0	0	0	0	0	0	0
HY/2009/15 & HY/2010/08	C7	0	0	0	0	0	0	0	0	0	0	0	0
<b>Total</b>		0	0	0	0	0	0	0	0	0	0	0	0

- Remarks: - The cessation of seawater intake operation for C6 was confirmed on 17 May 2011, the water monitoring at C6 was then terminated since 17 May 2011.
- WSD9 and WSD17 were implemented with respect to HK/2009/02 from 8 Feb 2012.
  - 4-week water quality monitoring at WSD9, WSD10, WSD15, WSD17, C8, C9 were completed on 6 Feb 2012.
  - C8 and C9 were implemented with respect to HY/2009/19 from 28 Jan 2012.
  - C8 & C9 was temporarily suspended on 30 March 2013 due to the marine works for Contract no. HY/2009/19 had been completed on 4 March 2013
  - WSD7 and WSD20 were temporarily suspended from 27 Apr 2012
  - C2, C3 C4e and C4w water quality monitoring station was temporarily suspended since 24 Apr 2013
  - C5e and C5w water quality monitoring station was temporarily suspended since 29 July 2013

- WSD21 water quality monitoring station was temporarily suspended since 12 March 2014
- Maintenance responsibility of silt screen C1, WSD19, P3, P4 and P5 are under Contract HK/2009/01.
- WSD9 and WSD17 water quality monitoring station was temporarily suspended since 8 September 2014 flood tide.
- Water quality monitoring for Windsor House Cooling (Station Ref: C7) was temporarily suspended since 22 October 2014 with respect to the diversion scheme and was resumed since 22 December 2014.
- The water monitoring station C1 shall be associated with Contract No. HK/2009/02 upon commencement of marine works under DP3 at WCR3 area

5.4.39. There was no action and limit level exceedance recorded in the reporting month.

5.4.40. Enhanced DO monitoring at 4 monitoring stations in Causeway Bay Typhoon Shelter and Ex-Public Cargo Works Area was conducted three days per week during the reporting period. The action and limit level exceedances of water quality monitoring are summarized in **Table 5.18**.

**Table 5.18 Summary of Enhanced Dissolved Oxygen Monitoring Exceedances in Reporting Month**

Contract no.	Water Monitoring Station	Mid-flood		Mid-ebb	
		DO		DO	
		AL	LL	AL	LL
HY/2009/15	C6	0	0	0	0
	C7	0	0	0	0
	Ex-WPCWA SW	0	1	0	5
	Ex-WPCWA SE	2	0	2	1
Total		2	1	2	6

5.4.41. There were 4 action level and 7 limit level exceedances of enhanced dissolved oxygen recorded in this reporting month. Investigation found that the exceedances were not related to Project works. The details of recorded exceedances can be referred to the **Section 6.4**.

5.4.42. In response to the Condition 2.18 of the Environmental Permit no. EP-356/2009 requiring that a silt curtain / impermeable barrier system be installed to channel water discharge flow from Culvert L to locations outside the embayment area, a proposed replacement of the requirement with additional dissolved oxygen monitoring has been conducted at three monitoring stations, namely A, B and C between the eastern seawall of Central Reclamation Phase III and the HKCEC Extension since November 2011 under EP-356/2009 so that DO level between the eastern seawall of Central Reclamation Phase II and the HKCEC extension could be continuously monitored. Details of additional DO monitoring results can be referred in **Appendix 5.4**.

- 5.4.43. With respect to the commencement of dredging works under HK/2012/08 and the installation of MTR precast protection unit, the enhanced water quality monitoring for Culvert L was temporarily suspended since 24 July 2013
- 5.4.44. With respect to the commencement of temporary reclamation works and seawall construction at Ex-PCWAW zone and diverted culvert extension, the location of the Enhance DO monitoring stations (Ex-PCWASW and Ex-PCWA SE) were finely adjusted to the PCWAE since 7 November 2014.

## 5.5 Waste Monitoring Results

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

- 5.5.1. No inert C&D waste and non- inert C&D waste disposed in this reporting month. Details of the waste flow table are summarized in **Table 5.19**.

**Table 5.19 Details of Waste Disposal for Contract no. HK/2009/01**

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup>	NIL	62116.405	TKO137, TM38
Inert C&D materials recycled, m <sup>3</sup>	NIL	5856.5	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	1673.69	SENT Landfill
Non-inert C&D materials recycled, kg	NIL	203993	N/A
Chemical waste disposed, kg	NIL	10250	N/A
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	NIL (Bulk Volume)	97428.2 (Bulk Volume)	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m <sup>3</sup>	NIL (Bulk Volume)	52250 (Bulk Volume)	East of Cha Chau
Dredged Sediment Requiring Type 3 – Special Treatment / Disposal contained in Geosynthetic Containers	NIL (Bulk Volume)	6773 (Bulk Volume)	East of Cha Chau

5.5.2. There were no marine sediment Type 1- Open Sea Disposal and no marine sediments Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal disposed in this reporting month.

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East

5.5.3. No inert C&D waste and Non-inert C&D waste disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.20**.

**Table 5.20 Details of Waste Disposal for Contract no. HK/2009/02**

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup>	NIL	276075.1	TKO137 / TM 38
Inert C&D materials recycled, m <sup>3</sup>	NIL	18161	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	1515.103	SENT Landfill
Non-inert C&D materials recycled, m <sup>3</sup>	N/A	N/A	N/A
Chemical waste disposed, kg	NIL	13860	SENT Landfill
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	NIL	244249 (Bulk volume)	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m <sup>3</sup>	NIL	146445* (Bulk volume)	East of Sha Chau

5.5.4. There was no marine sediment Type 1 – Open Sea Disposal (Dedicate Sties) and Type 1 Open Sea Disposal (Dedicate Sties) & Type 2 – Confined Marine Disposal disposed in this reporting month.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

5.5.5. No Inert C&D waste and no non- inert C&D waste disposed of in this reporting month. Details of the waste flow table are summarized in **Table 5.21**

**Table 5.21 Details of Waste Disposal for Contract no. HY/2009/15**

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds	Remarks
Inert C&D materials disposed, m <sup>3</sup>	NIL	141579.2	Tuen Mun Area 38	NIL
	NIL	65216	TKO137 FB	NIL
Inert C&D materials recycled, m <sup>3</sup>	NIL	304	Ex-PCWA	NIL
	NIL	111.9	TS4	NIL
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	252.2	SENT Landfill	NIL
Non-inert C&D materials recycled, kg	NIL	299361.5	N/A	NIL
Chemical waste disposed, kg	NIL	8,200	N/A	NIL
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	10774 (Bulk Volume)	137072 (Bulk Volume)	Cheung Chau South	Dredging from TCBR1E / TCBR1W / TCBR2/ TCBR3 / TCBR4 / Maintenance dredging
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m <sup>3</sup>	6112 (Bulk Volume)	307175* (Bulk Volume)	East of Sha Chau / South of the Brothers	Dredging from TCBR1E / TCBR1W / TCBR2/ TCBR3 / TCBR4 / Maintenance dredging
Marine Sediment (Type 3 – Special Treatment / Disposal contained in Geosynthetic Containers) m <sup>3</sup>	NIL (Bulk Volume)	12640 (Bulk Volume)	East of Sha Chau / South of the Brothers	Dredging from TCBR1W / Maintenance dredging
Marine Sediment (Type 2 – Confined Marine Disposal), m <sup>3</sup>	NIL	9350 (Bulk Volume)	East of Sha Chau	Dredging from Eastern Breakwater of CBTS
Marine Sediment (Type 1 – Open Sea Disposal) , m <sup>3</sup>	NIL (Bulk Volume)	600 (Bulk Volume)	East Sha Chau / South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement
Marine Sediment (Type 2– Confined Marine Disposal) , m <sup>3</sup>	NIL (Bulk Volume)	14,780 (Bulk Volume)	South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement
Marine Sediment (Type 3 – Special Treatment / Disposal contained in Geosynehetic	NIL (Bulk Volume)	2,760 (Bulk Volume)	South of The Brothers	Dredging from Phase 3 Mooring Re-arrangement

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds	Remarks
Containers) , m3				

\* Remarks: The cumulative quantity of Type 1 – Open Sea Disposal (Delicate Sites) & Type 2 – Confined Marine Disposal has been updated in this reporting month.

- 5.5.6. There were Type 1 Open Sea Disposal and Type 1 Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal disposed in this reporting month.

Contract no. HY/2009/19 –Central- WanChai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 5.5.7. No inert C&D waste and non-inert C&D waste disposed in this reporting month. Details of the waste flow table are summarized in **Table 5.22**.

**Table 5.22 Details of Waste Disposal for Contract no. HY/2009/19**

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup>	NIL	355921.04	TM38
Inert C&D materials recycled, m <sup>3</sup>	NIL	59367	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	1068.6	N/A
Non-inert C&D materials recycled, kg	NIL	333.14	N/A
Chemical waste disposed, L	NIL	2.12	N/A
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	NIL	162	South Cheung Chau
Marine Sediment (Type 2 – Confined Marine Disposal) , m <sup>3</sup>	NIL	681	East Sha Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m3	NIL	4976.00	

- 5.5.8. There was no marine sediment Type1- Open Sea Disposal and there was no Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal generated were disposed in this reporting month.

Contract no. HK/2012/08 –Wan Chai Development Phase II – Central- Wan Chai Bypass at

Wan Chai West

- 5.5.9. There was no Inert C&D waste and no non-inert C&D waste disposed in this reporting month. Details of the waste flow table are summarized in **Table 5.23**.

**Table 5.23 Details of Waste Disposal for Contract no. HK/2012/08**

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup>	NIL	4131	TM38
Inert C&D materials recycled, m <sup>3</sup>	NIL	NIL	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	315	N/A
Non-inert C&D materials recycled, kg	NIL	NIL	N/A
Chemical waste disposed, L	NIL	NIL	N/A
Marine Sediment (Type 1 – Open Sea Disposal), m <sup>3</sup>	NIL (Bulk volume)	31759* (Bulk volume)	South of Cheung Chau
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal) , m3	NIL (Bulk volume)	108485 (Bulk volume)	South of The Brothers (from 27 Aug 2013 onwards)

\*Remarks: Contractor clarified that there were no Marine Sediment (Type 1 – Open Sea Disposal) disposed in July reporting month. The cumulative quantity has been updated in this reporting month.

- 5.5.10. There were no Marine Sediment Type 1 – Open Sea Disposal and marine sediment Type 1 – Open Sea Disposal (Delicate Sites) & Type 2 – Confined Marine Disposal disposed in this reporting month.

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8)

- 5.5.11. Inert C&D waste was disposed and no non-inert C&D waste disposed in this reporting month. Details of the waste flow table are summarized in **Table 5.24**

**Table 5.24 Details of Waste Disposal for Contract no. HY/2010/08**

Waste Type	Quantity this month	Cumulative Quantity-to-Date	Disposal / Dumping Grounds
Inert C&D materials disposed, m <sup>3</sup>	147948.9	267660.2	N/A
Inert C&D materials recycled, m <sup>3</sup>	NIL	NIL	N/A
Non-inert C&D materials disposed, m <sup>3</sup>	NIL	NIL	N/A
Non-inert C&D materials recycled, kg	NIL	NIL	N/A
Chemical waste disposed, L	NIL	NIL	N/A
Marine Sediment (Type 1 –	NIL	55290	South Cheung Chau /

<b>Waste Type</b>	<b>Quantity this month</b>	<b>Cumulative Quantity-to-Date</b>	<b>Disposal / Dumping Grounds</b>
Open Sea Disposal)			Brothers Island *
Marine Sediment (Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine disposal)	NIL	27760	Brothers Island
Marine Sediment (Type 3 – Special Treatment)	NIL	7780	Brothers Island

Remarks: Under the condition of EP/MD/15-169, dredged sediment required to dispose at South of the Brothers since 9 Feb 2015.

- 5.5.12. There was no Type 1 – Open Sea Disposal, Type 3 – Special Treatment and Type 1 – Open Sea Disposal (Dedicate Sites) & Type 2 – Confined Marine Disposal disposed in this reporting month.

## 6. Compliance Audit

6.0.1. The Event Action Plan for construction noise, air quality and water quality are presented in Appendix 6.1.

### 6.1 Noise Monitoring

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

6.1.1 No exceedance was recorded in the reporting month.

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

6.1.2 No exceedance was recorded in the reporting month.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

6.1.3 No exceedance was recorded in the reporting month.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

6.1.4 No exceedance was recorded in the reporting month.

Contract no. HY/2010/08 – Central-Wanchai Bypass – Tunnel (Slip Road 8 Section)

6.1.5 No exceedance was recorded in the reporting month.

### 6.2 Real-time noise Monitoring

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

6.2.1. No limit level exceedance was recorded in the reporting month.

### 6.3 Air Monitoring

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

6.3.1 No exceedance was recorded in the reporting month.

Contract no. HK/2009/02 – Wan Chai Development Phase II – Central – Wan Chai Bypass at Wan Chai East (CWB Tunnel)

6.3.2 No exceedance was recorded in the reporting month.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

6.3.3 No exceedance was recorded in the reporting month.

6.3.4 No action and limit level was recorded for odour patrol during this reporting month.

Contract no. HY/2009/19 – Central – Wanchai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

6.2.1. One action level exceedance during 24hr TSP monitoring was recorded at monitoring station CMA2a – Causeway Bay Community Centre on 26 August 2015 and two action level exceedances during 1hr TSP monitoring exceedances were recorded at monitoring station CMA2a – Causeway Bay Community Centre on 27 August 2015 in the reporting month.

6.2.2. External renovation undertaken at Causeway Bay Community Centre on 26, 27 August 2015 by non-CWB Contractor was considered as the major contribution to the air quality impact and the exceedances were considered as non-Project related.

Contract no. HK/2012/08 Wan Chai Development Phase II - Central-Wan Chai Bypass at Wan Chai West

6.2.3. No exceedance was recorded in the reporting month.

Contract no. HY/2010/08 – Central-Wanchai Bypass – Tunnel (Slip Road 8 Section)

6.2.4. No exceedance was recorded in the reporting month.

#### 6.4 Water Quality Monitoring

Contract no. HK/2009/01 - Wan Chai Development Phase II – Central –Wanchai Bypass at HKCEC

6.4.1 No exceedance was recorded in the reporting month.

Contract no. HK/2009/02 - Wan Chai Development Phase II – Central – Wan Chai Bypass at WanChai East

6.4.2 No exceedance was recorded in the reporting month.

Contract no. HY/2009/15 - Central-Wanchai Bypass – Tunnel (Causeway Bay Typhoon Shelter Section)

6.4.3 There were occasionally DO exceedance was recorded at Ex-WPCWA SW on 3, 5, 14, 17, 19 and 27 August 2015 in the reporting month.

6.4.4 After checking with contractor, despite excavated mud transshipment was conducted at Ex-WPCWA on 3, 5, 14, 17, 19 and 27 August 2015, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted and no exceedance was recorded on the subsequent monitoring, the exceedances were considered not related to the Project works.

6.4.5 There was occasionally DO exceedance was recorded at Ex-WPCWA SE on 14, 17, 19 and 27 August 2015 in the reporting month.

- 6.4.6 After checking with contractor, despite excavated mud transshipment was conducted at Ex-WPCWA on 14, 17, 19 and 27 August 2015, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted, the exceedance was considered not related to the Project works. Nevertheless, the contractor was reminded to increase the frequency of floating refuses collection and reposition floating curtain to eliminate any potential effect to the water quality within the area. The DO level at the concerned location was subsequently resumed on 14 August 2015 flood tide and 21 August 2015 flood tide.

Contract no. HY/2009/19- Central- Wan Chai Bypass Tunnel (North Point Section) and Island Eastern Corridor Link

- 6.4.7 No exceedance was recorded in this reporting month.

Contract no. HK/2012/08- Wan Chai Development Phase II – Central- Wan Chai Bypass at Wan Chai West

- 6.4.8 No exceedance was recorded in this reporting month.

Contract no. HY/2010/08 –Central - Wan Chai Bypass (CWB) –Tunnel (Slip Road 8)

- 6.4.9 No exceedance was recorded in this reporting month.

**6.5 Review of the Reasons for and the Implications of Non-compliance**

- 6.5.1 There was no non-compliance from the site audits in the reporting period. The observations and recommendations made in each individual site audit session were presented in Section 8.
- 6.5.2 No non-compliances from monitoring was recorded in the reporting month.

**6.6 Summary of action taken in the event of and follow-up on non-compliance**

- 6.6.1 There was no particular action taken since no non-compliance was recorded from the site audits in the reporting period.

## **7. Cumulative Construction Impact due to the Concurrent Projects**

- 7.0.1. According to Condition 3.4 of the EP-356/2009, this section addresses the relevant cumulative construction impact due to the concurrent activities of the current projects including the Central Reclamation Phase III, Central-Wanchai Bypass and Island Eastern Corridor Link projects.
- 7.0.2. According to the Final EM&A Report of Central Reclamation Phase III (CRIII) for Contract HK 12/02, the major construction activities were completed by end of January 2014 and no construction activities were undertaken thereafter and the water quality monitoring was completed in October 2011 and no Project-related exceedance was recorded for air and noise monitoring. It can be concluded that cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was insignificant.
- 7.0.3. According to the construction programme of Central-Wanchai Bypass at Wanchai West at the Central Reclamation Phase III area, construction of ELS and pipe pile wall, road works and drainage were performed in August 2015 reporting month. As no project related exceedance were recorded during the reporting period, cumulative construction impact due to the concurrent activities of the current projects with the Central Reclamation Phase III (CRIII) was considered as insignificant.
- 7.0.4. According to the construction programme of Wan Chai Development Phase II, Central-Wan Chai Bypass and Island Eastern Corridor Link projects, the major construction activities under Wan Chai Development Phase II were tunnel works, ELS works and culvert construction at Wan Chai East and removal of L-shape wall, D-wall construction and ELS works at Wan Chai West. The major construction activities under Central-Wan Chai Bypass and Island Eastern Corridor Link Projects were bridge construction and road works at Central Interchange, ELS works at Ex-PCWAW, ELS works and retaining wall construction at Victoria Park, D- wall construction and ELS works at TS3, IEC demolition and tunnel works at North Point area in the reporting month.
- 7.0.5. No significant air impact from construction activities was anticipated in the reporting month. Besides, no project related exceedance was recorded during the air and noise environmental monitoring events in the reporting month. Thus, it is evaluated that the cumulative construction impact from the concurrent projects including Central Reclamation Phase III (CRIII), Wan Chai Development Phase II (WDII), Central-WanChai Bypass (CWB), Island Eastern Corridor Link projects (IECL) was insignificant.

**8. Environmental Site Audit**

8.0.1. During this reporting month, weekly environmental site audits were conducted for Contracts no. HK/2009/01, HK/2009/02, HY/2009/15, HY/2009/19, HK/2012/08 and HY/2010/08. No non-conformance was identified during the site audits.

8.0.2. Five site inspections for Contract no. HK/2009/01 were conducted on 29 July, 5, 12, 20 and 26 August 2015 in reporting month. Results of these inspections and outcomes are summarized in **Table 8.1**.

**Table 8.1 Summary of Environmental Inspections for Contract no. HK/2009/01**

Item	Date	Observations	Action taken by Contractor	Outcome
150729_01	29-Jul-15	The drainage system at Stage 3 shall be properly maintain to avoid any direct effluent discharge to the water channel at Expo Drive East	The U channel was blocked and no direct effluent discharge was further observed.	Completion as observed on 5 August 2015
150805_1	5-Aug-15	Drip tray shall be provided for oil container at Stage 3.	Drip tray as provided for oil container at Stage 3.	Completion as observed on 12 August 2015

8.0.3. Five site inspections for Contract no. HK/2009/02 were carried out on 30 July, 6, 13, 19 and 27 August 2015 in reporting month. No particular finding was observed in this reporting month. Results of these inspections and outcomes are summarized in **Table 8.2**.

**Table 8.2 Summary of Environmental Inspections for Contract no. HK/2009/02**

Item	Date	Observations	Action taken by Contractor	Outcome
150813_01	13-Aug-15	Drip tray shall be provided for oil containers at Portion 3&4	Oil containers has been removed	Completion as observed on 19 August 2015
150819_01	19-Aug-15	Breaker shall be properly covered with acoustic material at Portion 2.	Breaker was properly covered with acoustic material at Portion 2.	Completion as observed on 27 August 2015
150827_01	27-Aug-15	Drip tray shall be provided for oil containers at Portion 3 & 4	Drip tray was provided for oil containers at Portion 3 & 4	Completion as observed on 2 September 2015
150827_02	27-Aug-15	Chemical waste shall be properly handled and stored in chemical storage at Portion 3 & 4	Chemical waste was removed at Portion 3 &4	Completion as observed on 2 September 2015
150827_03	27-Aug-15	Breaker shall be covered with acoustic material when operating at Portion 3&4	Breaker was properly covered with acoustic material at Portion 3 & 4	Completion as observed on 2 September 2015

8.0.4. Five site inspections for Contract no. HY/2009/15 were carried out on 28 July, 5, 11, 18 and 25 August 2015 in reporting month. The results of these inspections and outcomes are summarized in **Table 8.3**.

**Table 8.3 Summary of Environmental Inspections for Contract no. HY/2009/15**

Item	Date	Observations	Action taken by Contractor	Outcome
150805_1	5-Aug-2015	Sand/ mud deposit around surface drainage shall be cleaned to avoid blocking the drainage flow and subsequent contaminated discharge to nearby waters via culvert sediment trap with effluent collection point shall be provided to the concerned drainage (Ex-Helipad of Ex-PCWA)	Sand/ mud deposit was removed and sediment trap was installed within the drainage.	Completed as observed on 11 August 2015
150811_1	11-Aug-2015	Mud residue shall not directly washed into nearby waters using water stream ( EX-PCWA North)	No further washing was observed and mud residue was cleared	Completed as observed on 18 August 2015
150811_2	11-Aug-2015	Floating refuses trapped within the construction area should be cleaned ( EX-PCWA SE)	Floating refuses have been cleared	Completed as observed on 18 August 2015
150818_1	18-Aug-2015	Clear the leaked oil as chemical waste and provide regular maintenance to machinery on-site ( EX-PCWAW)	Leaked oil was cleared as chemical waste.	Completed as observed on 18 August 2015
150825_1	25-Aug-2015	Provide drip tray to chemical containers (Ex-PCWA)	Drip tray was provided	Completed as observed on 25 August 2015

- 8.0.5. Five site inspections for Contract no. HY/2009/19 were carried out on 29 July, 5, 12, 19 and 26 August 2015 in reporting month. Results of these inspections and outcomes are summarized in **Table 8.4**.

**Table 8.4 Summary of Environmental Inspections for Contract no. HY/2009/19**

Item	Date	Observations	Action taken by Contractor	Outcome
150812_1	12/8/2015	Temporary noise barrier shall be provided to saw cutting process ( Main Section)	Temporary noise barrier was provided to saw cutting process	Completion as observed on 19 August 2015

- 8.0.6. Five site inspections for Contract no. HK/2012/08 were carried out on 28 July, 4, 11, 18 and 25 August 2015 in this reporting period. The results of these inspections and outcomes are summarized in **Table 8.5**

**Table 8.5 Summary of Environmental Inspections for Contract no. HK/2012/08**

Item	Date	Observations	Action taken by Contractor	Outcome
150728_01	28-Jul-15	Drip tray shall be provided for oil container at Portion 1A	Drip tray is provided for oil container	Completion as observed on 4

Item	Date	Observations	Action taken by Contractor	Outcome
				August 2015
150728_02	28-Jul-15	Adequate mitigation measure shall be provided at the rock bund of the water channel to mitigate the observed muddy runoff and dispersion.	Runoff control has been implemented and no muddy runoff was further observed.	Completion as observed on 4 August 2015
150804_01	4-Aug-15	Wheel washing shall be strengthened and controlled to avoid generation of muddy trail at Gate near HK Expo Centre.	Street cleaning and wheel washing has properly implemented at Gate Exit.	Completion as observed on 11 August 2015
150804_02	4-Aug-15	Silt curtain shall be fully extended to seabed level and enclosed the excavated area at Zone D	Silt curtain is properly deployed and maintained at Zone D.	Completion as observed on 11 August 2015
150804_03	4-Aug-15	Drip tray shall be provided for oil container on site	Drip tray is provided for oil containers.	Completion as observed on 11 August 2015
150811_01	11-Aug-15	Floating refuses at HKCEC2W area shall be collected.	Floating refuses has collected at HKCEC2W area.	Completion as observed on 18 August 2015
150818_01	18-Aug-15	Wheel washing shall be strengthened at Gate Exit on Expo Drive West to avoid muddy trail on public road.	Wheel washing was conducted properly and no muddy trail was observed on the public road.	Completion as observed on 1 September 2015
150825_01	25-Aug-15	Drip tray shall be provided for oil container at Portion 1A.	Oil container was removed.	Completion as observed on 1 September 2015

8.0.7. Five site inspections for Contract no. HY/2010/08 were carried out on 31 July, 6, 14, 20 and 27 August 2015 in this reporting period. The results of these inspections and outcomes are summarized in **Table 8.6**

**Table 8.6 Summary of Environmental Inspections for Contract no. HY/2010/08**

Item	Date	Observations	Action taken by Contractor	Outcome
150702_1	2-Jul-15	Hoarding provided along the covered pedestrian walkway shall be of at least 2.4m tall according to the APCO requirement (TS3)	--	Pending for Contractor follow up action

150731_1	31-Jul-15	Muddy seepage was observed at southwest corner of TS3. The contractor was mitigate the source of seepage and provide additional silt curtain to and muddy dispersion ( SW corner of TS3)	Additional silt curtain was provided and reinforcement was implemented to mitigate the muddy seepage	Completion as observed on 6 August 2015
150731_2	31-Jul-15	Covering shall be provided to cement bags stored on site	Covering was provided	Completion as observed on 6 August 2015
150806_1	6-Aug-15	Leaked oil shall be cleared as chemical waste and drip tray shall be provided to oil containers (TS3)	Leaked oil was cleared as chemical waste	Completion as observed on 14 August 2015
150814_1	14-Aug-15	Measures shall be provided to rectify the muddy seepage at the southwest area of TS3 (TS3)	The silt curtain condition was improved to avoid seepage	Completion as observed on 27 August 2015
150814_2	14-Aug-15	Protective wrapping fencing should be provided to retained trees near works area (Victoria Park)	Protecting wrapping was provided to the concerned trees	Completion as observed on 27 August 2015
150827_1	27-Aug-15	Proper three sides and top cover shall be provided to mixing station (TS3)	Three sides and top cover was provided to grouting station	Completion as observed on 2 September 2015

**9. Complaints, Notification of Summons and Prosecution**

9.0.1. No environmental complaint was received in the reporting month.

9.0.2. The details of cumulative complaint log and updated summary of complaints are presented in **Appendix 9.1**

9.0.3. Cumulative statistic on complaints and successful prosecutions are summarized in **Table 9.1** and **Table 9.2** respectively.

**Table 9.1 Cumulative Statistics on Complaints**

Reporting Period	No. of Complaints
Commencement works (Mar 2010) to last reporting month	37
August 2015	0
<b>Total</b>	<b>37</b>

**Table 9.2 Cumulative Statistics on Successful Prosecutions**

Environmental Parameters	Cumulative No. Brought Forward	No. of Successful Prosecutions this month (Offence Date)	Cumulative No. Project-to-Date
Air	-	0	0
Noise	-	0	0
Water	-	0	0
Waste	-	0	0
<b>Total</b>	-	<b>0</b>	<b>0</b>

**10. Conclusion**

10.0.1. The EM&A programme was carried out in accordance with the EM&A Manual requirements, minor alterations to the programme proposed were made in response to changing circumstances.

10.0.2. The scheduled construction activities and the recommended mitigation measures for the coming month are listed in **Table 10.1**.



**Table 10.1 Construction Activities and Recommended Mitigation Measures in Coming Reporting Month**

Contract No.	Key Construction Works	Recommended Mitigation Measures
HK/2009/01	<ul style="list-style-type: none"> <li>Nil</li> </ul>	<ul style="list-style-type: none"> <li>Nil</li> </ul>
HK/2009/02	<ul style="list-style-type: none"> <li>Construction of Seawall at WCR3</li> <li>Reclamation at WCR3</li> <li>Demolition of remaining part of existing Wan Chai Ferry Pier</li> </ul>	<ul style="list-style-type: none"> <li>Nil</li> </ul>
HY/2009/15	<ul style="list-style-type: none"> <li>Reinstatement of vertical seawall at TPCWAE</li> </ul>	<ul style="list-style-type: none"> <li>Daily visual inspection of silt screen and silt curtain to ensure its operation properly</li> <li>Implement silt curtain in accordance with the associated plans submitted to EPD.</li> </ul>
HY/2009/19	<ul style="list-style-type: none"> <li>Nil</li> </ul>	<ul style="list-style-type: none"> <li>To space out noisy equipment and position as far as possible from sensitive receiver.</li> </ul>
HK/2012/08	<ul style="list-style-type: none"> <li>Dry dock construction</li> <li>Installation of pipe pile wall</li> <li>Removal of temporary piling platform for culvert diversion</li> <li>Construction of culvert</li> </ul>	<ul style="list-style-type: none"> <li>To conform the installation and setting as in the silt screen and silt curtain deployment plan</li> <li>To space out noisy equipment and position as far as possible from sensitive receiver.</li> <li>Daily visual inspection of silt screen and silt curtain to ensure its operation properly</li> </ul>
HY/2010/08	<ul style="list-style-type: none"> <li>Diversion pipe maintenance</li> </ul>	<ul style="list-style-type: none"> <li>To conform the installation and setting as in the silt screen and silt curtain deployment plan</li> <li>Daily visual inspection of silt screen and silt curtain to ensure its operation properly</li> </ul>



***Figure 2.1***

***Project Layout***

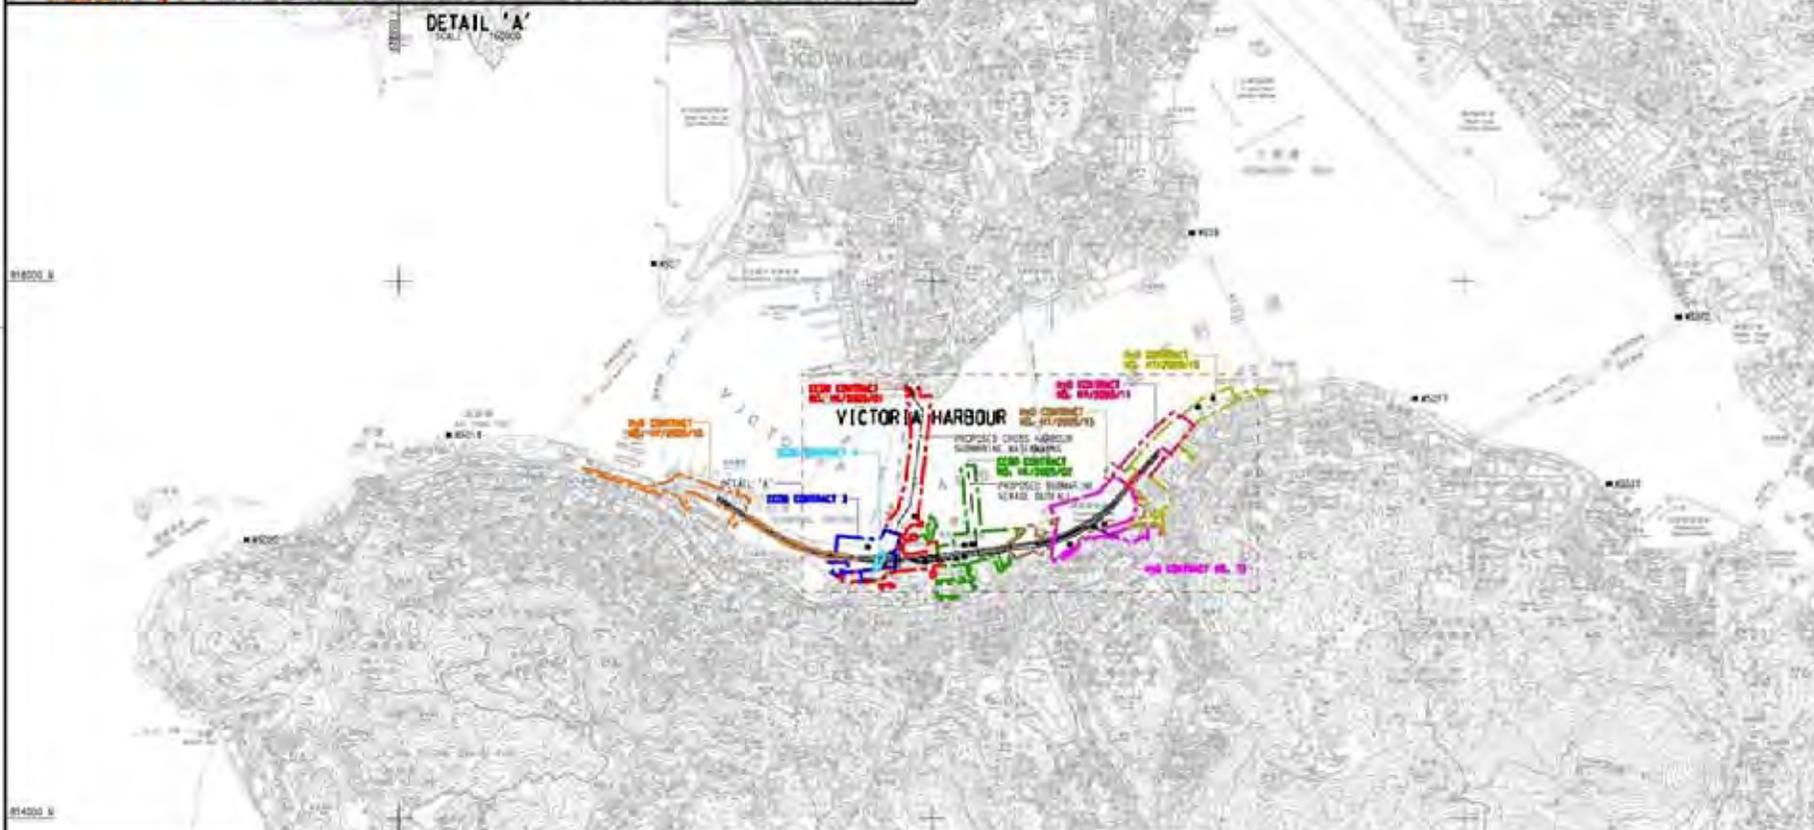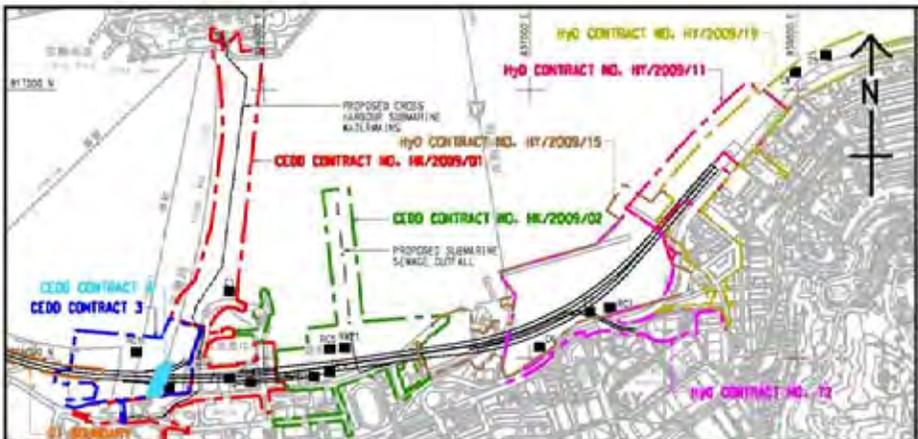

- LEGEND:**
- WATER QUALITY MONITORING STATIONS
- COOLING WATER INTAKES**
- 01 WONG KONG CONVENTION AND EXHIBITION CENTRE EXTENSION
  - 02 TELECOM HOUSE AND ACADEMY 1 ON WILSON ROAD / SAITLWAY CENTRE
  - 03 WONG KONG CONVENTION AND EXHIBITION CENTRE PHASE 1
  - 04 WAN CHAI TOWER AND GREAT WALL CENTRE
  - 05 SUN HANG KAI CENTRE
  - 06 PROPOSED EXHIBITION STATION / WORLD TRADE CENTRE
  - 07 WINDSOR HOUSE
  - 08 CITY SQUARE
  - 09 PROVIDENT CENTRE
  - 102 PROPOSED HERPA EXTENSION
  - 103 SUN HANG KAI CENTRE / REPRODUCTION
  - 107 WINDSOR HOUSE (TEMPORARY REPRODUCTION)
- WSD SALT WATER INTAKE**
- #201 WAN CHAI
  - #401 WAN CHAI (REPRODUCTION)
  - #501 CANTON SQUARE
  - #601 SA. SAN
  - #620 CHA KWO LING
  - #621 SA. SAN ISD
  - #622 SCARLET BAY
  - #623 SHILOH BAY
  - #624 KENNEDY TOWN

DESIGNATED PROJECT'S TOP	WORK CONTRACT	DESIGNATED PROJECT NUMBER	COMPLETION (APPROXIMATE)
SP1 - CENTRAL WAN CHAI STYASS WORKS INCLUDING 15 ROAD TUNNEL AND SLOPE ROADS	CEDD CONTRACT NO. HK/2009/01	SP1 - SP3 - SP6	APRIL 2010
SP2 - ROAD P2 AND OTHER ROADS (PRIMARY & DISTRICT DISTRIBUTION ROADS)	CEDD CONTRACT NO. HK/2009/02	SP1 - SP3 - SP5	APRIL 2010
SP3 - PERMANENT AND TEMPORARY ROAD MAINTENANCE WORKS INCLUDING ASSOCIATED DRAINAGE WORKS IN WAN CHAI DEVELOPMENT PHASE 1T / WSD1T AREA	CEDD CONTRACT 3	SP1 - SP3	END 2011
SP4 - TEMPORARY BRIDGE-SHELTER 1 (SP4 NOT TO BE IMPLEMENTED)	CEDD CONTRACT 4	SP1 - SP3	END 2011
SP5 - WAN CHAI EAST SEWAGE DUTY ALL	CEDD CONTRACT 5	SP3	2010
SP6 - DISINFECTING FOR THE CROSS-HARBOUR WATER MAINS	HYD CONTRACT NO. HY/2009/11	SP3	18 AUGUST 2010
	HYD CONTRACT NO. HY/2009/15	SP1 - SP3	SEPTEMBER 2010
	HYD CONTRACT NO. HY/2009/16	SP1	OCTOBER 2010
	HYD CONTRACT NO. HY/2009/18	SP1	NOVEMBER 2010
	HYD CONTRACT 12	SP1 - SP3	MID 2010



**CEDD** 土木工程發展局  
Civil Engineering and Development Department

**WAN CHAI DEVELOPMENT PHASE II**

WAN CHAI DEVELOPMENT PHASE II, PHASE CENTRE - SANITARY FITTINGS REVISIONS AND TESTING WORKS (STAGE 1)

**LOCATIONS OF WATER QUALITY MONITORING STATIONS**


**AECOM**

PROJECT NUMBER: **60041297/C5/SK001**

DATE: 2010	SCALE: 1:10000	DATE: 2010	SCALE: 1:10000
BY: [Signature]	BY: [Signature]	BY: [Signature]	BY: [Signature]
CHECKED: [Signature]	CHECKED: [Signature]	CHECKED: [Signature]	CHECKED: [Signature]

© COPYRIGHT RESERVED



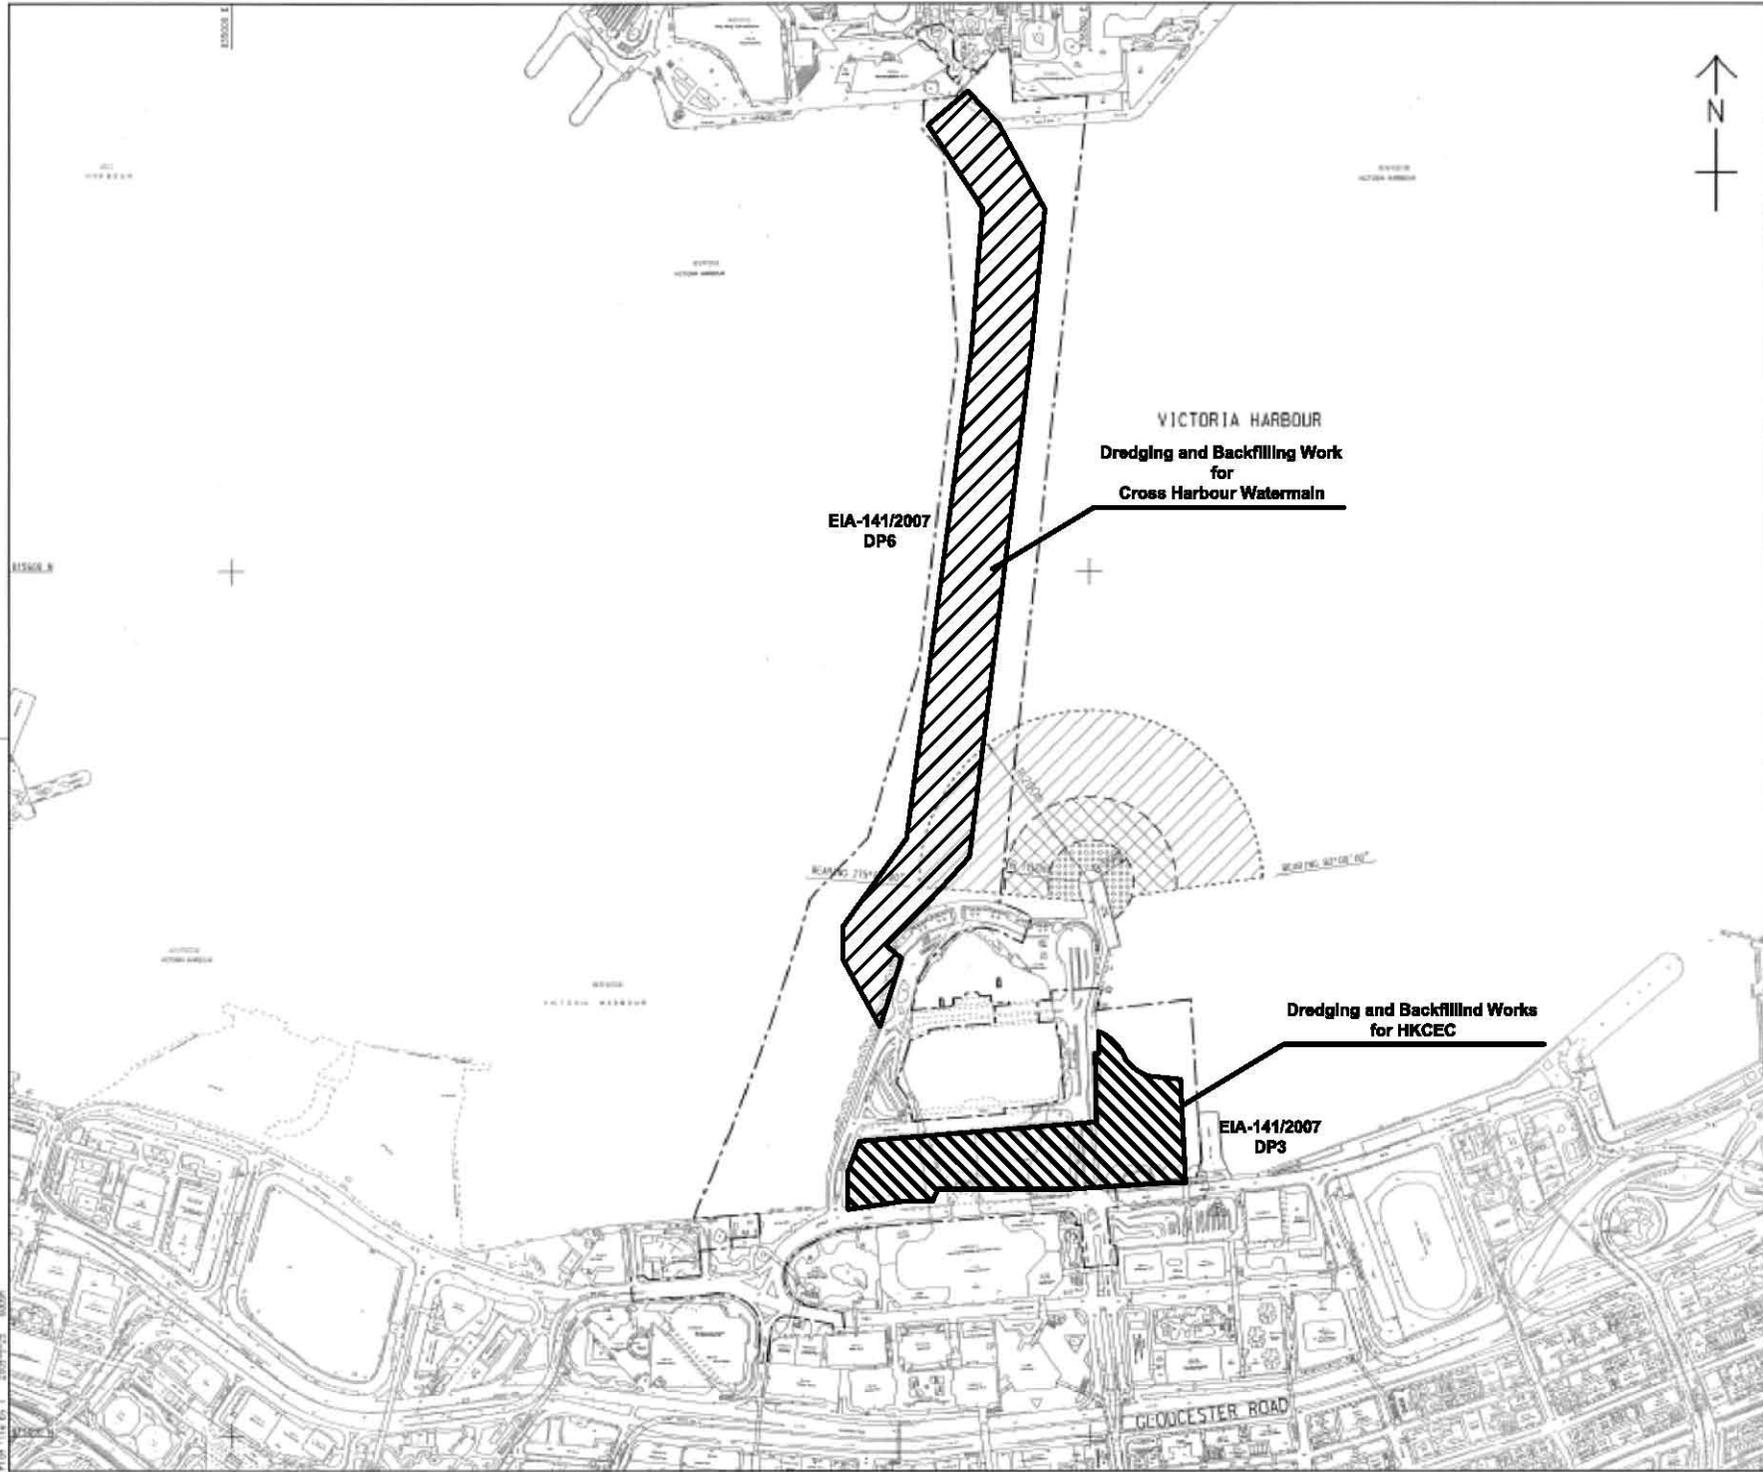

LOCATION PLAN  
SCALE 1 : 5000

- NOTES:
1. ALL DIMENSIONS ARE IN METRES UNLESS OTHERWISE NOTED.
  2. THE RESTRICTION ZONE IS THIS DRAWING WILL COME INTO EFFECT AFTER THE OPERATION OF THE GOVERNMENT HULLING AT EDP/D/D/E LAST.

LEGEND:

	CONTRACT BOUNDARY
	WORKING RESTRICTION ZONE
	NAVIGATION AND WORKING RESTRICTION ZONE
	WORKING BARGE, NAVIGATION AND WORKING RESTRICTION ZONE

TENDER ADDENDUM NO. 4	DATE: 21/11/09
TENDER ADDENDUM NO. 1	DATE: 21/11/09
TENDER DRAWING	DATE: 21/11/09

CEDD 土木工程發展署  
Civil Engineering and Development Department

WAN CHAI DEVELOPMENT PHASE II  
WAN CHAI DEVELOPMENT PHASE II -  
KONG KONG CONVENTION AND EXHIBITION CENTRE  
**RESTRICTED ZONE FOR  
CONSTRUCTION VESSELS**  
(Contract no: HK/2009/01)


**AECOM**

DRGNO. 60041297/C1/100/1010B	DATE: 16/2/2009/01
SCALE: AS 1:8000	COPYRIGHT RESERVED



INSET 'A'  
SCALE 1:1000

CENTRAL DISTRICT

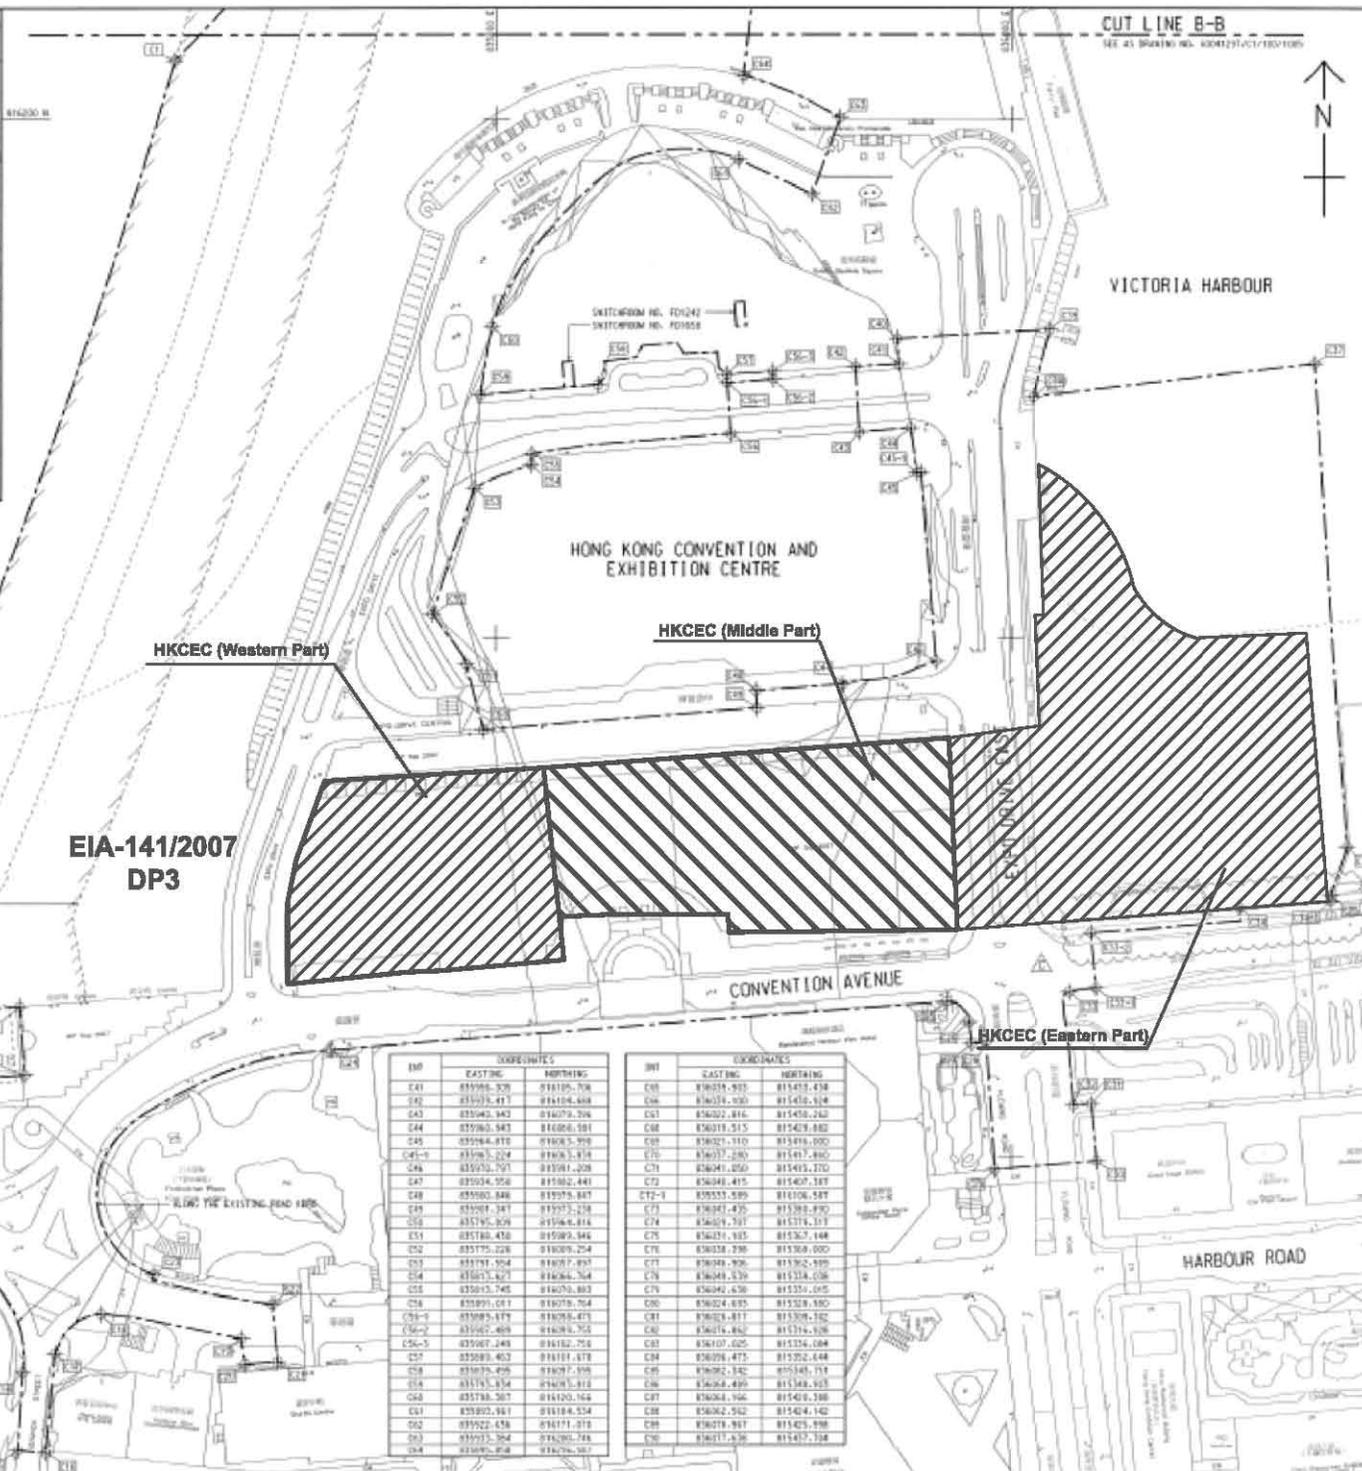

EIA-141/2007  
DP3

INT	COORDINATES	
	EASTING	NORTHING
C41	835986.528	818105.708
C42	835973.417	818104.468
C43	835963.943	818079.706
C44	835963.543	818086.581
C45	835964.818	818085.528
C46	835965.504	818085.514
C46	835973.757	818081.208
C47	835974.956	818082.441
C48	835980.846	818079.887
C49	835981.347	818077.238
C50	835976.828	818066.814
C51	835988.478	818080.846
C52	835975.226	818089.224
C53	835973.504	818077.897
C54	835973.627	818084.764
C55	835973.745	818079.883
C56	835991.071	818078.764
C56-1	835995.679	818078.873
C56-2	835982.468	818078.765
C56-3	835987.248	818182.758
C57	835983.403	818181.878
C58	835978.498	818077.198
C59	835978.574	818081.818
C60	835978.587	818120.744
C61	835993.881	818184.524
C62	835923.434	818171.812
C63	835973.584	818080.748
C64	835973.818	818078.507

INT	COORDINATES	
	EASTING	NORTHING
C65	836028.933	818473.438
C66	836034.000	818473.614
C67	836022.816	818473.240
C68	836019.515	818473.882
C69	836021.110	818474.000
C70	836027.289	818471.880
C71	836041.050	818493.270
C72	836048.415	818487.187
C72-1	835555.589	818106.587
C73	836047.435	818385.890
C74	836049.797	818374.107
C75	836024.185	818382.148
C76	836038.298	818388.000
C77	836048.906	818382.898
C78	836048.439	818374.038
C79	836042.438	818351.045
C80	836024.635	818328.880
C81	836028.417	818308.182
C82	836028.882	818378.148
C83	836107.025	818326.084
C84	836098.473	818322.444
C85	836092.342	818348.714
C86	836084.499	818348.925
C87	836084.196	818348.388
C88	836082.512	818348.142
C89	836078.987	818345.898
C90	836077.438	818347.198



KEY PLAN  
SCALE 1:10000


NOTE:  
1. FOR NOTES & LEGEND, REFER TO DRAWING NO. 60041297/C1/100/1006.

INT	COORDINATES	
	EASTING	NORTHING
C1	836879.285	818222.559
C2	836879.271	818222.299
C3	836874.561	818228.425
C4	836871.020	818231.014
C5	836882.482	818229.522
C6	836881.584	818218.612
C7	836886.545	818215.197
C8	836886.199	818207.147
C9	836886.433	818202.247
C10	836891.082	818207.050
C11	836885.389	818208.075
C12	836871.486	818208.107
C13	836923.468	818204.817
C14	836886.433	818217.122
C15	836874.289	818208.500
C16	836875.195	818205.525
C17	836888.138	818204.441
C18	836846.085	818208.816
C19	836871.421	818205.587
C20	836902.537	818220.881
C21	836915.285	818217.484
C22	836913.182	818207.442
C23	836827.086	818209.074
C24	836926.984	818203.670
C25	836915.280	818208.251
C26	836881.447	818212.286
C27	836904.025	818203.896
C28	836906.218	818204.442
C29	836901.523	818206.180
C30	836883.781	818208.447
C31	836837.216	818228.470
C32	836824.142	818225.117
C33	836821.081	818205.482
C34	836826.290	818204.700
C35	836827.428	818203.286
C36	836888.187	818201.280
C36-1	836824.812	818208.093
C36-2	836824.747	818203.285
C36-3	836828.850	818219.194
C37	836818.190	818208.037
C38	836828.810	818207.289
C39	836818.906	818207.080
C40	836825.682	818215.512

C	TENDER ADDENDUM NO.4	SHW/1/1/SEP/08
B	TENDER ADDENDUM NO.2	SHW/1/1/SEP/08
A	TENDER ADDENDUM NO.1	SHW/1/1/SEP/08
-	TENDER DRAWING	SHW/1/1/SEP/08


**土木工程發展署**  
 Civil Engineering and Development Department  
**WAN CHAI DEVELOPMENT PHASE II**  
 WAI CHAI DEVELOPMENT PHASE II -  
 CENTRAL WAI CHAI DEVELOPMENT  
 HONG KONG CONVENTION AND EXHIBITION CENTRE  
**SITE BOUNDARY SETTING OUT PLAN**  
 (Contract no. HK/2009/01)

**AECOM**  
 DRGNO. 60041297/C1/100/1006C  
 SHEET NO. 1 OF 1  
 DATE: 08/2009/01  
 DRAWN BY: JAC  
 CHECKED BY: JAC  
 SCALE: AS SHOWN  
 COPYRIGHT RESERVED

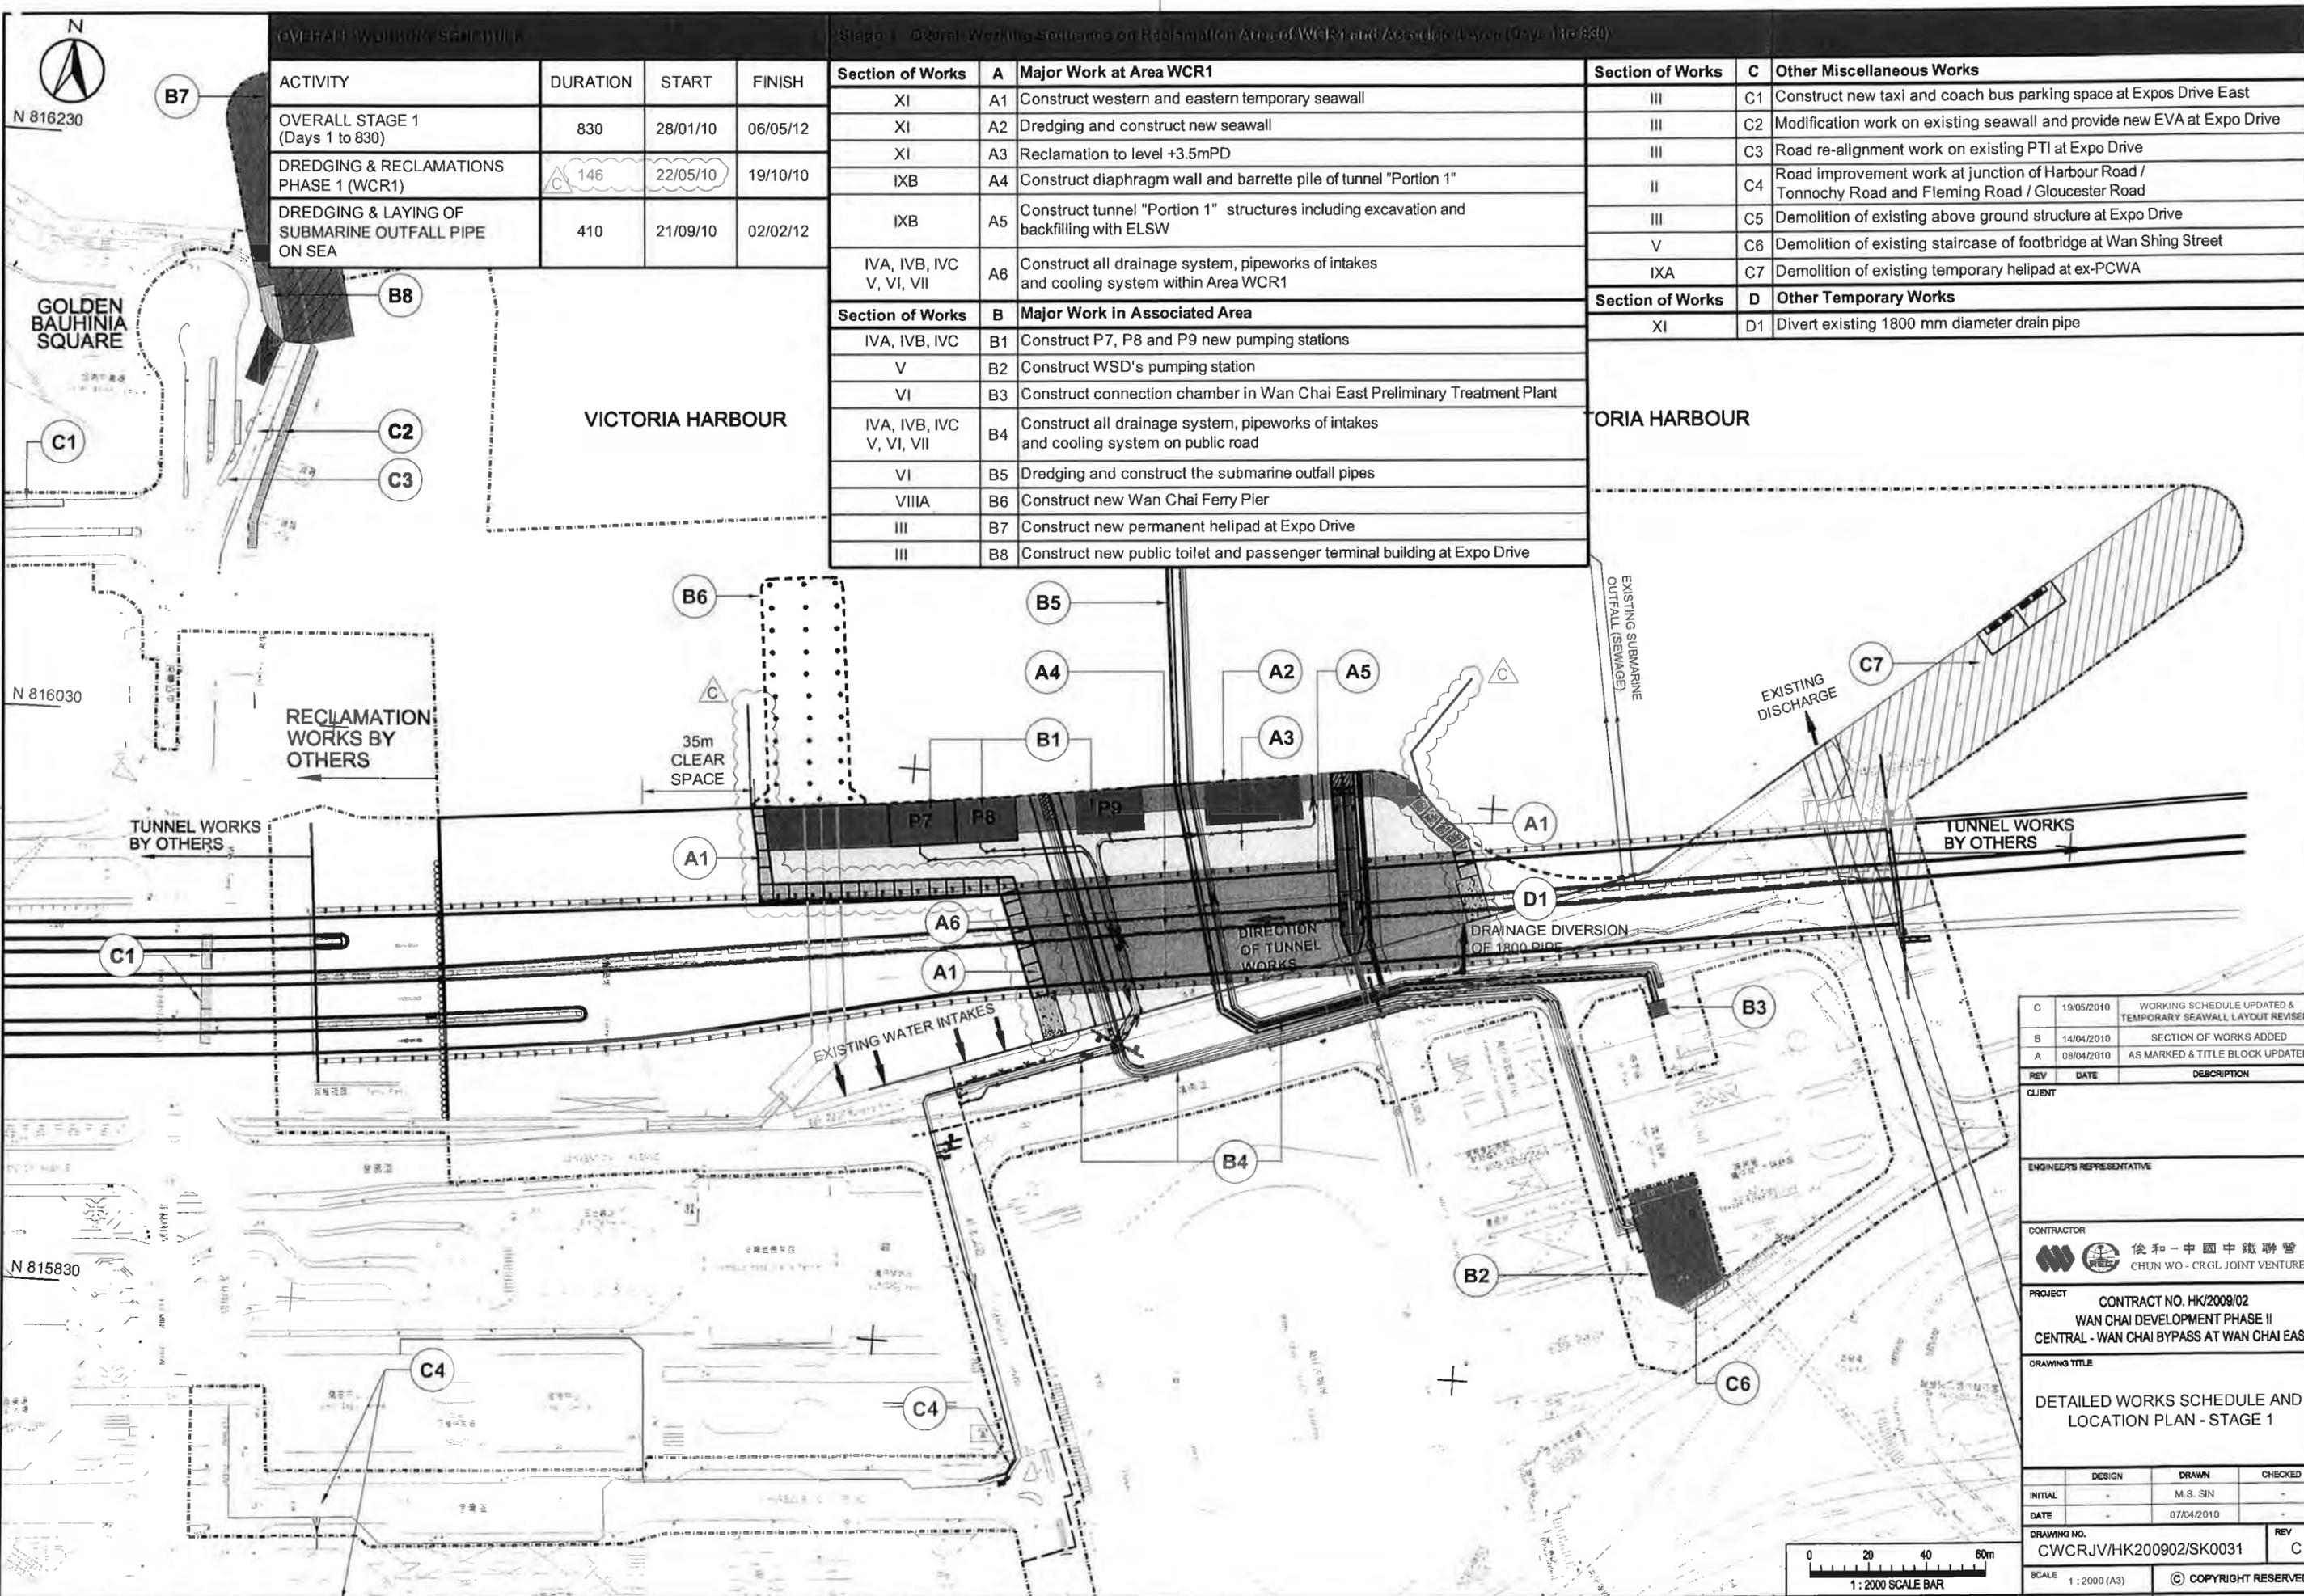

**OVERALL WORKING SCHEDULE**

ACTIVITY	DURATION	START	FINISH
OVERALL STAGE 1 (Days 1 to 830)	830	28/01/10	06/05/12
DREDGING & RECLAMATIONS PHASE 1 (WCR1)	146	22/05/10	19/10/10
DREDGING & LAYING OF SUBMARINE OUTFALL PIPE ON SEA	410	21/09/10	02/02/12

**Stage 1 - Overall Working Schedules on Reclamation Area of WCR1 and Associated Area (Days 1 to 830)**

Section of Works	A	Major Work at Area WCR1
XI	A1	Construct western and eastern temporary seawall
XI	A2	Dredging and construct new seawall
XI	A3	Reclamation to level +3.5mPD
IXB	A4	Construct diaphragm wall and barrette pile of tunnel "Portion 1"
IXB	A5	Construct tunnel "Portion 1" structures including excavation and backfilling with ELSW
IVA, IVB, IVC, V, VI, VII	A6	Construct all drainage system, pipeworks of intakes and cooling system within Area WCR1
Section of Works	B	Major Work in Associated Area
IVA, IVB, IVC	B1	Construct P7, P8 and P9 new pumping stations
V	B2	Construct WSD's pumping station
VI	B3	Construct connection chamber in Wan Chai East Preliminary Treatment Plant
IVA, IVB, IVC, V, VI, VII	B4	Construct all drainage system, pipeworks of intakes and cooling system on public road
VI	B5	Dredging and construct the submarine outfall pipes
VIIIA	B6	Construct new Wan Chai Ferry Pier
III	B7	Construct new permanent helipad at Expo Drive
III	B8	Construct new public toilet and passenger terminal building at Expo Drive

Section of Works	C	Other Miscellaneous Works
III	C1	Construct new taxi and coach bus parking space at Expos Drive East
III	C2	Modification work on existing seawall and provide new EVA at Expo Drive
III	C3	Road re-alignment work on existing PTI at Expo Drive
II	C4	Road improvement work at junction of Harbour Road / Tonnochy Road and Fleming Road / Gloucester Road
III	C5	Demolition of existing above ground structure at Expo Drive
V	C6	Demolition of existing staircase of footbridge at Wan Shing Street
IXA	C7	Demolition of existing temporary helipad at ex-PCWA
Section of Works	D	Other Temporary Works
XI	D1	Divert existing 1800 mm diameter drain pipe

REV	DATE	DESCRIPTION
C	19/05/2010	WORKING SCHEDULE UPDATED & TEMPORARY SEAWALL LAYOUT REVISED
B	14/04/2010	SECTION OF WORKS ADDED
A	08/04/2010	AS MARKED & TITLE BLOCK UPDATED

CLIENT  
ENGINEER'S REPRESENTATIVE


CONTRACTOR  

 俊和-中國中鐵聯營  
 CHUN WO - CRGL JOINT VENTURE

PROJECT  
 CONTRACT NO. HK/2009/02  
 WAN CHAI DEVELOPMENT PHASE II  
 CENTRAL - WAN CHAI BYPASS AT WAN CHAI EAST

DRAWING TITLE  
 DETAILED WORKS SCHEDULE AND  
 LOCATION PLAN - STAGE 1

DESIGN	DRAWN	CHECKED
INITIAL	M.S. SIN	
DATE	07/04/2010	
DRAWING NO.	CWCRJV/HK200902/SK0031	REV C
SCALE	1:2000 (A3)	© COPYRIGHT RESERVED





圖例：  
LEGEND:

-  地界範圍  
SITE BOUNDARY
-  園林綠化平台  
LANDSCAPED DECK
-  主幹道隧道  
TRUNK ROAD TUNNEL
-  擬建高架道路  
PROPOSED ELEVATED CARRIAGEWAY
-  現有高架行車道將予拆卸  
EXISTING ELEVATED CARRIAGEWAY TO BE DEMOLISHED
-  現有高架行車道將予拆卸及重建  
EXISTING ELEVATED CARRIAGEWAY TO BE DEMOLISHED AND RECONSTRUCTED



維多利亞海港 ×  
VICTORIA HARBOUR

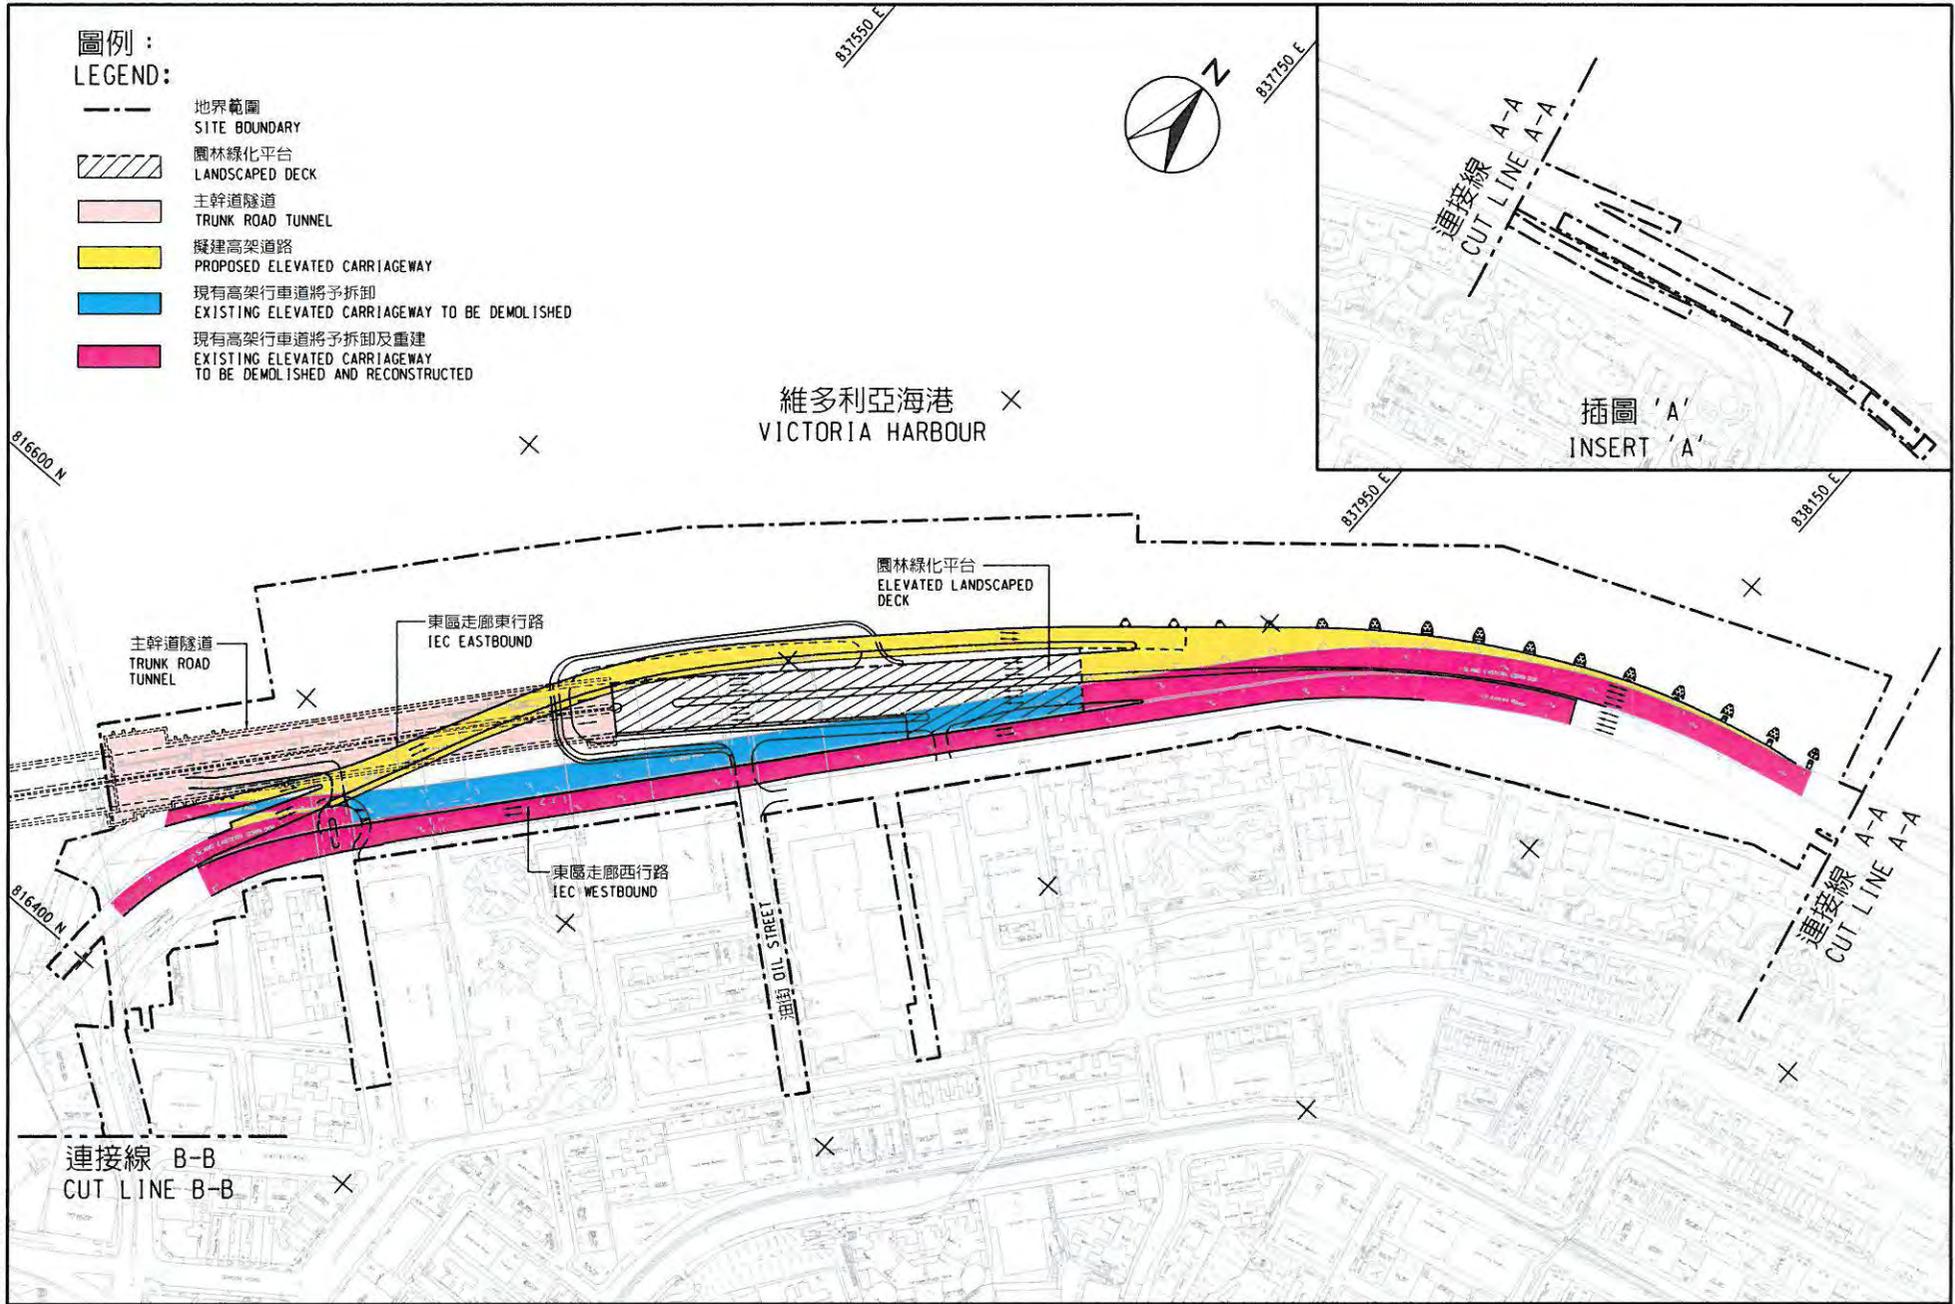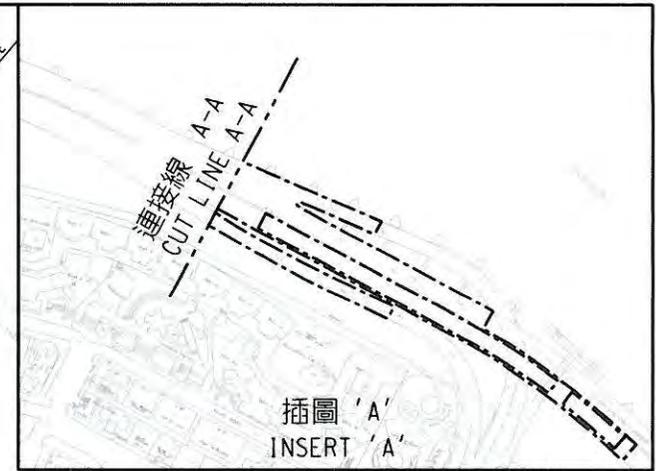

合約編號 HY/2009/19 - 中環灣仔繞道 - 北角段隧道及東區走廊連接路

CONTRACT NO. HY/2009/19 - CENTRAL-WAN CHAI BYPASS - TUNNEL (NORTH POINT SECTION) AND ISLAND EASTERN CORRIDOR LINK

SCALE 1 : 3000




港口  
HONG KONG PORT



LEGEND:



WORKS AREA



DREDGING AREA FOR  
MITIGATION OF ODOUR(DP3)



SITE BOUNDARY



中環繞路工程(粵海)有限公司  
CHINA STATE CONSTRUCTION ENGR. (HONG KONG) LTD.


Highways Department  
CONTRACT NO. HY/2009/15  
CENTRAL-WAN CHAI BYPASS - TUNNEL  
(CAUSEWAY BAY TYPHOON  
SHELTER SECTION)

TITLE  
LOCATION PLAN OF WORKS AREA

DRG. NO.  
CWB/EPD/001B

SCALE  
1:1000 @ A0  
DIMENSIONS ARE IN  
MILLIMETERS

SIMBO  
COPYRIGHT RESERVED

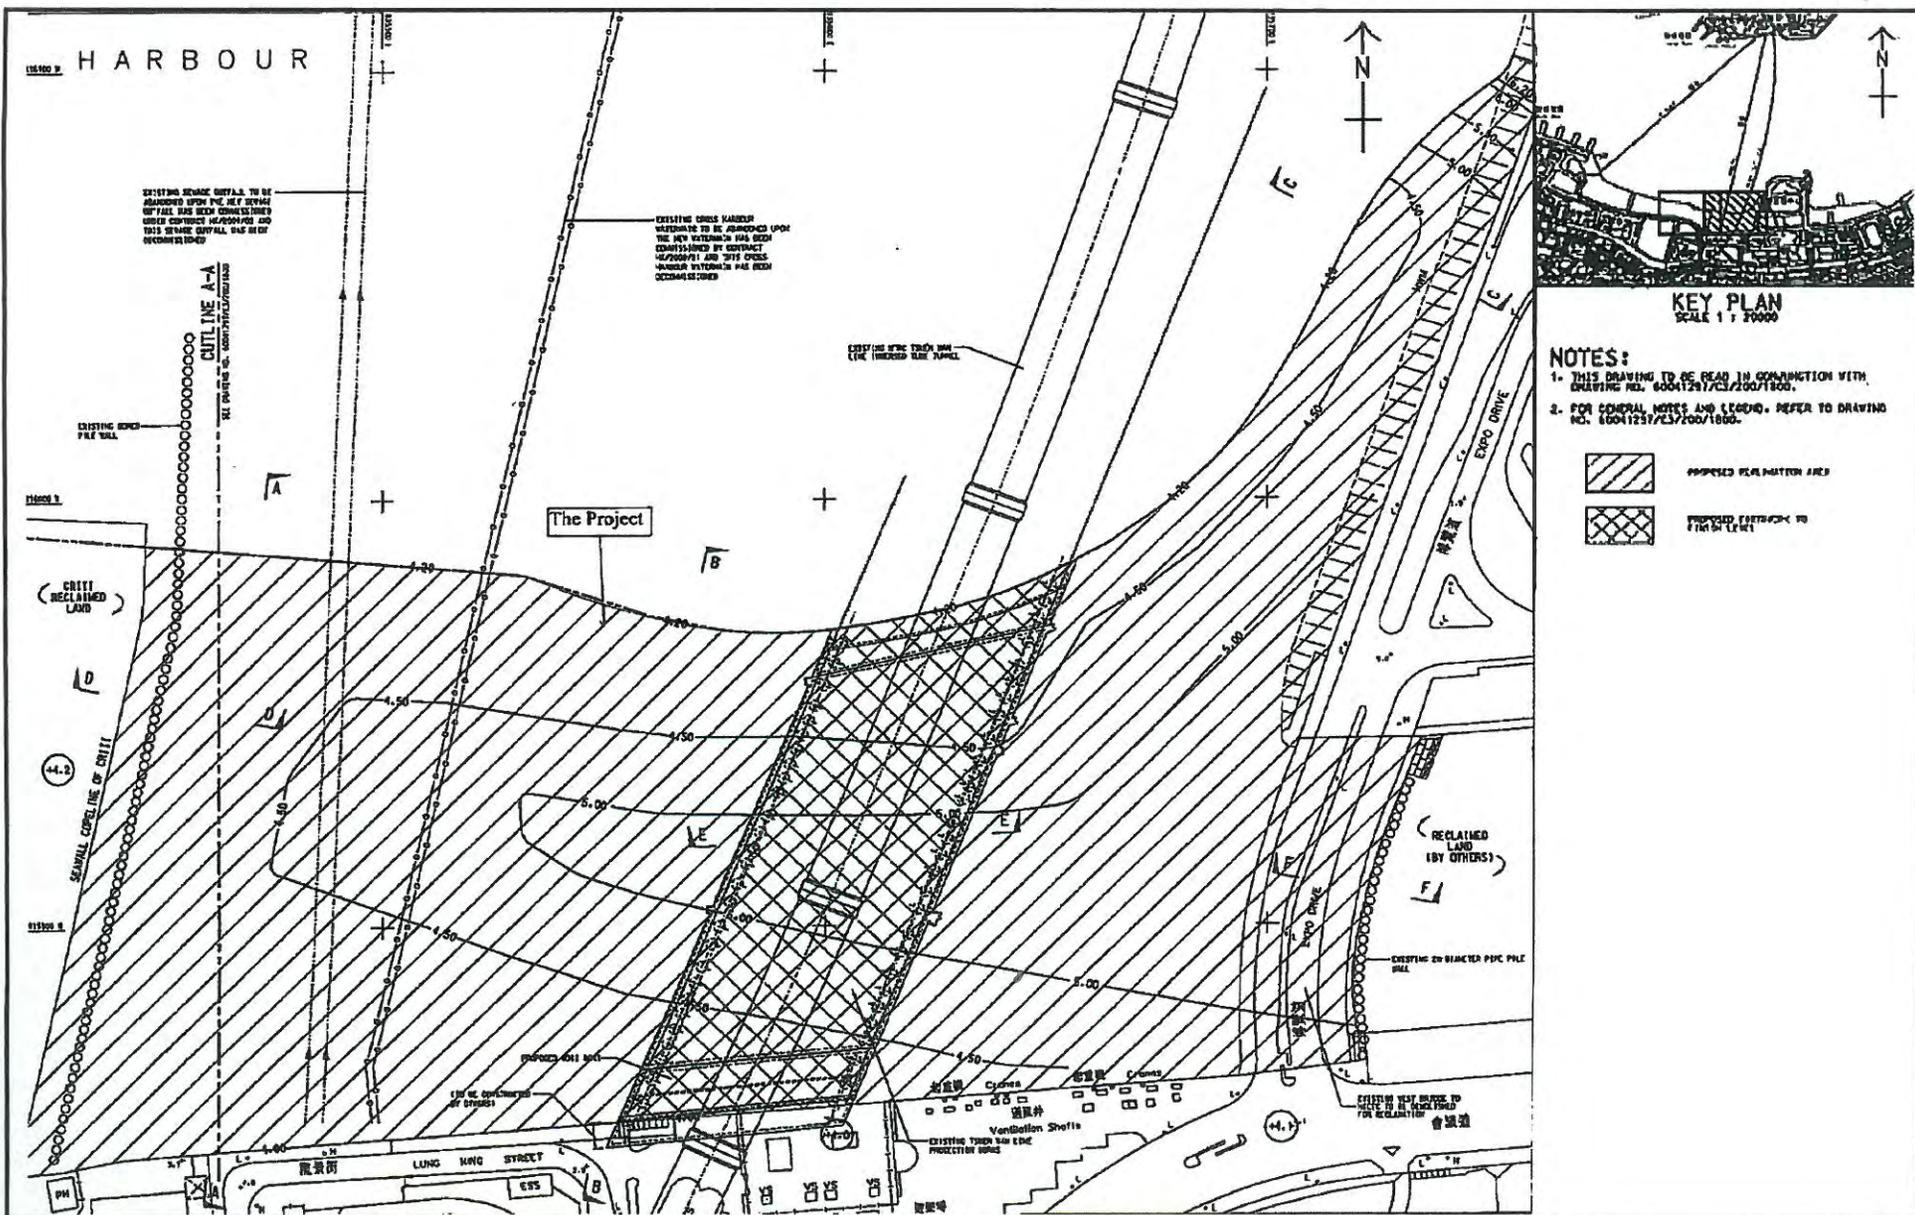

**Project Title: Wan Chai Development Phase II – Central Wan Chai Bypass at Wan Chai West (Contract No. HK/2012/08) – Marine Works**  
**工程項目名稱: 灣仔發展計劃第二期 - 中環灣仔繞道-灣仔西段(合約編號:HK/2012/08)-海事工程**  
**Environmental Permit No. : FEP-06/356/2009**  
**環境許可證編號 : FEP-06/356/2009**

**Figure 1b : General Layout of the Project**  
**圖 1b : 工程項目佈局圖**

(This figure was prepared based on Figure 1b of Application for Further Environmental Permit (Application No.: FEP 145/2013))  
 (本圖是根據申請新的環境許可證(申請書編號 FEP-145/2013) 圖 1b 編製)



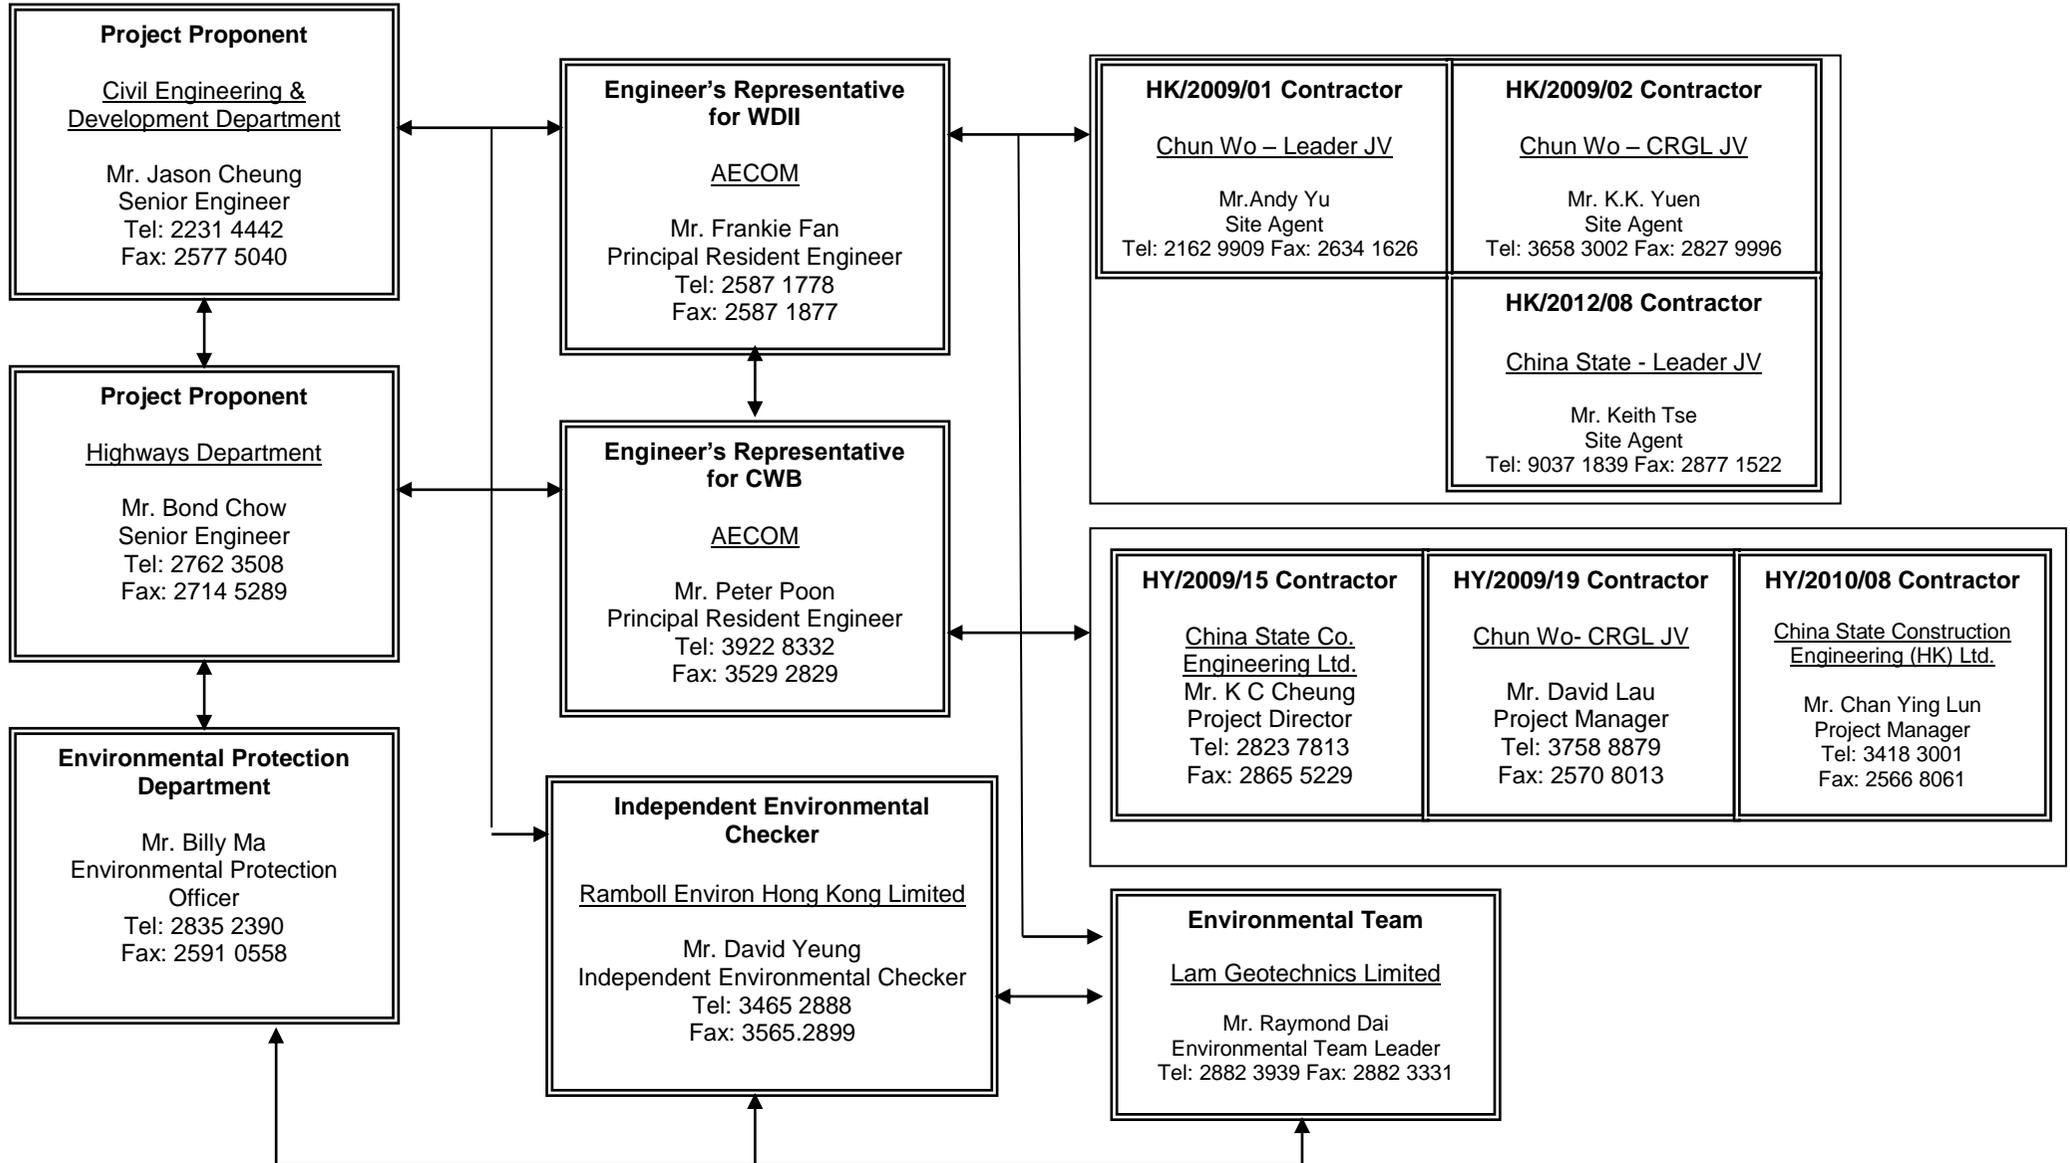


***Figure 2.2***

***Project Organization Chart***




**Project Organization Chart**






***Figure 4.1***

***Locations of Monitoring Stations***

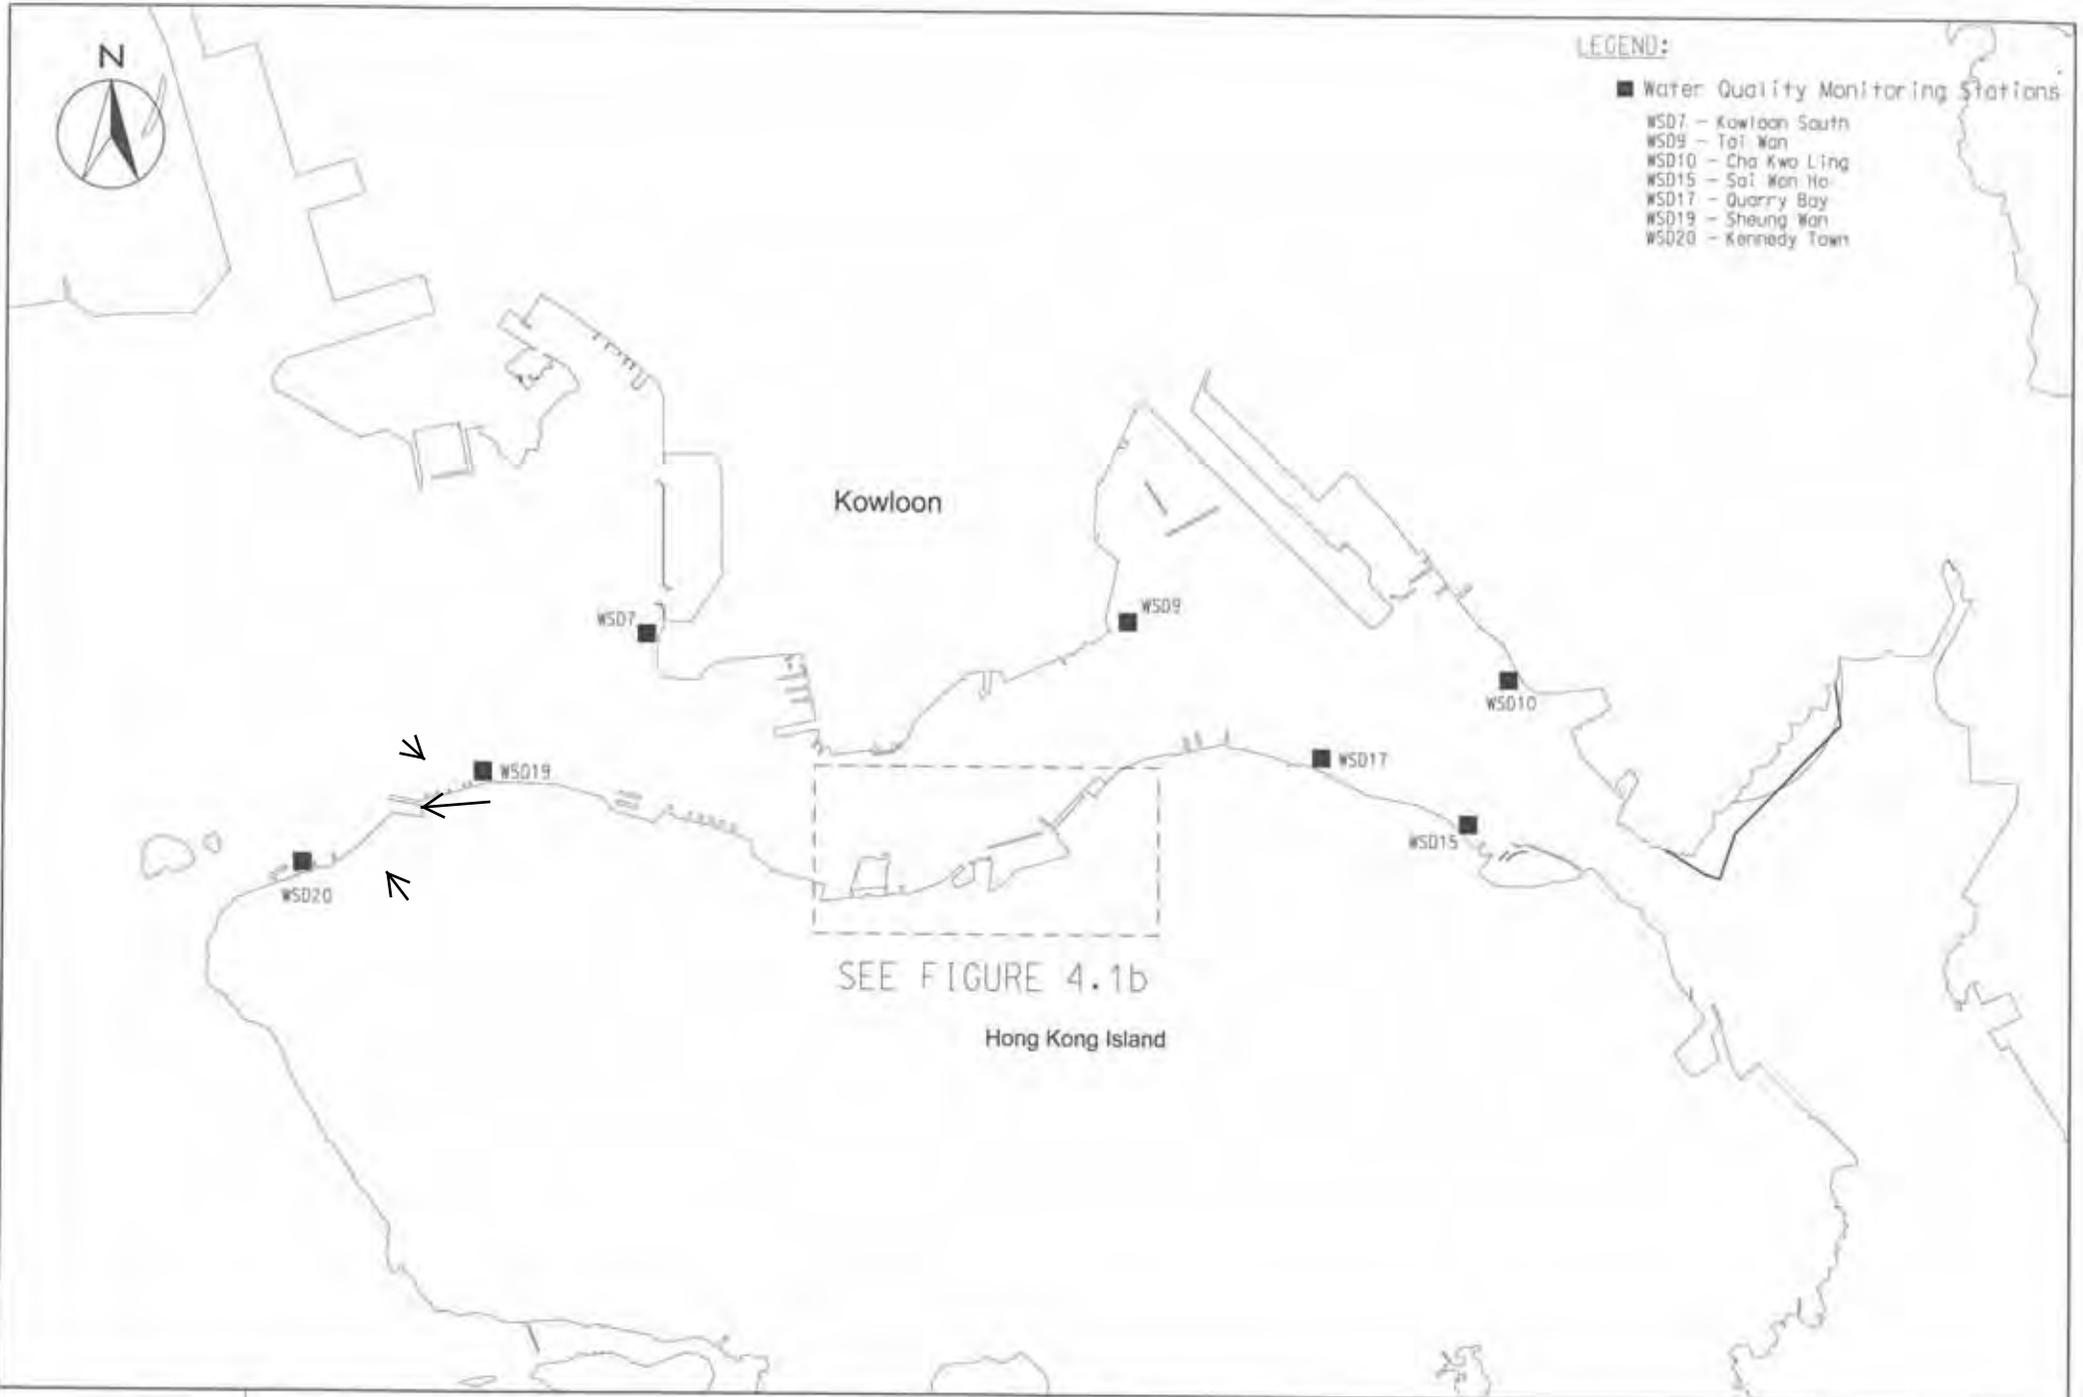

### Legend


- Noise Monitoring Station
- Air Monitoring Station
- ▲ Real-time Noise Monitoring Station

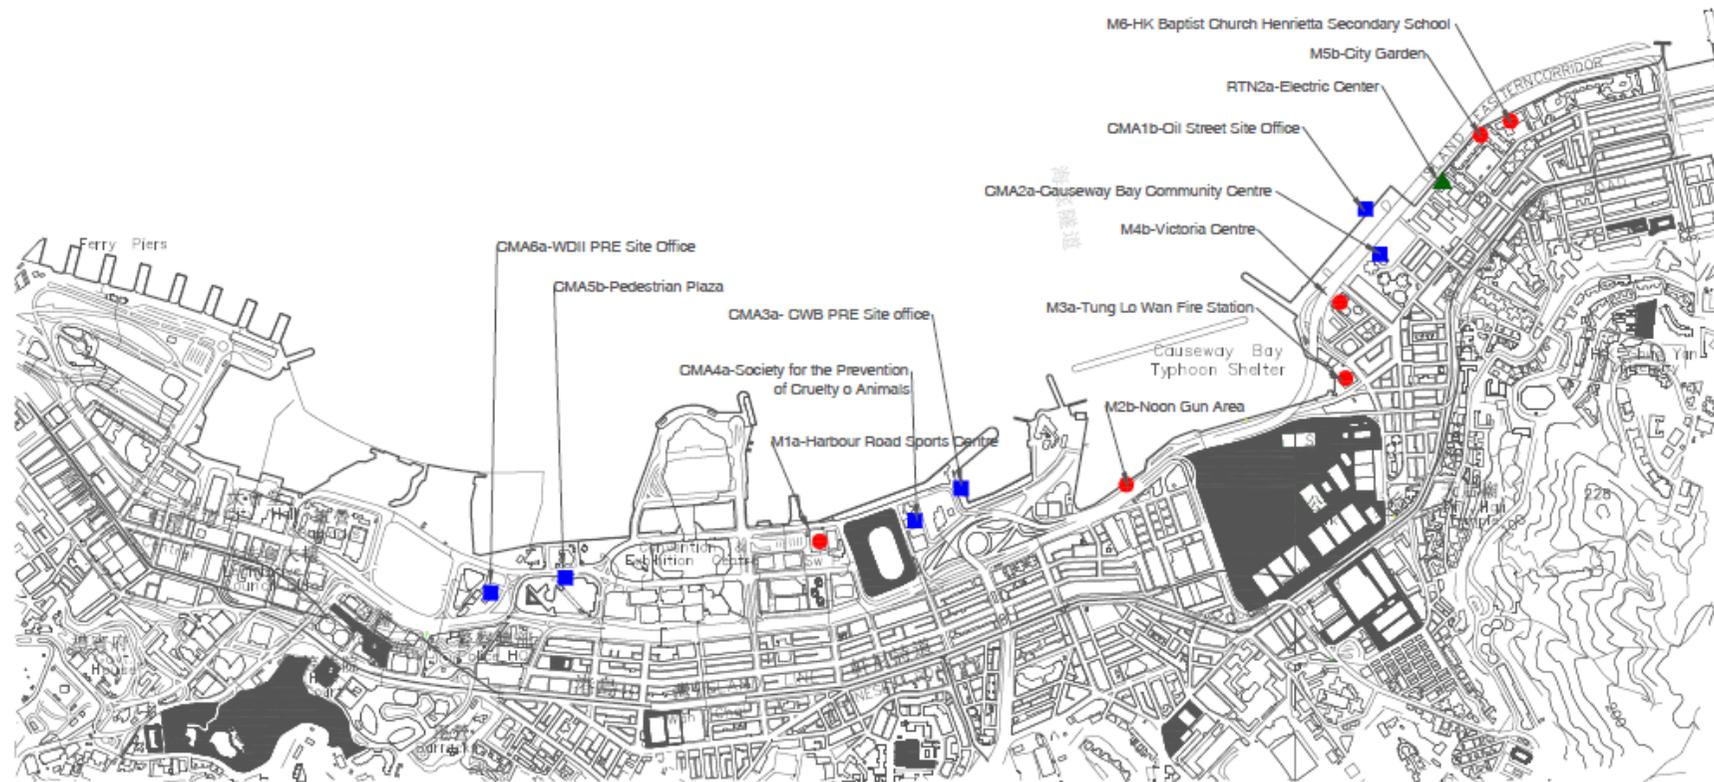

## LOCATIONS OF ENVIRONMENTAL MONITORING STATIONS


Legend

● Enhanced DO Monitoring Station

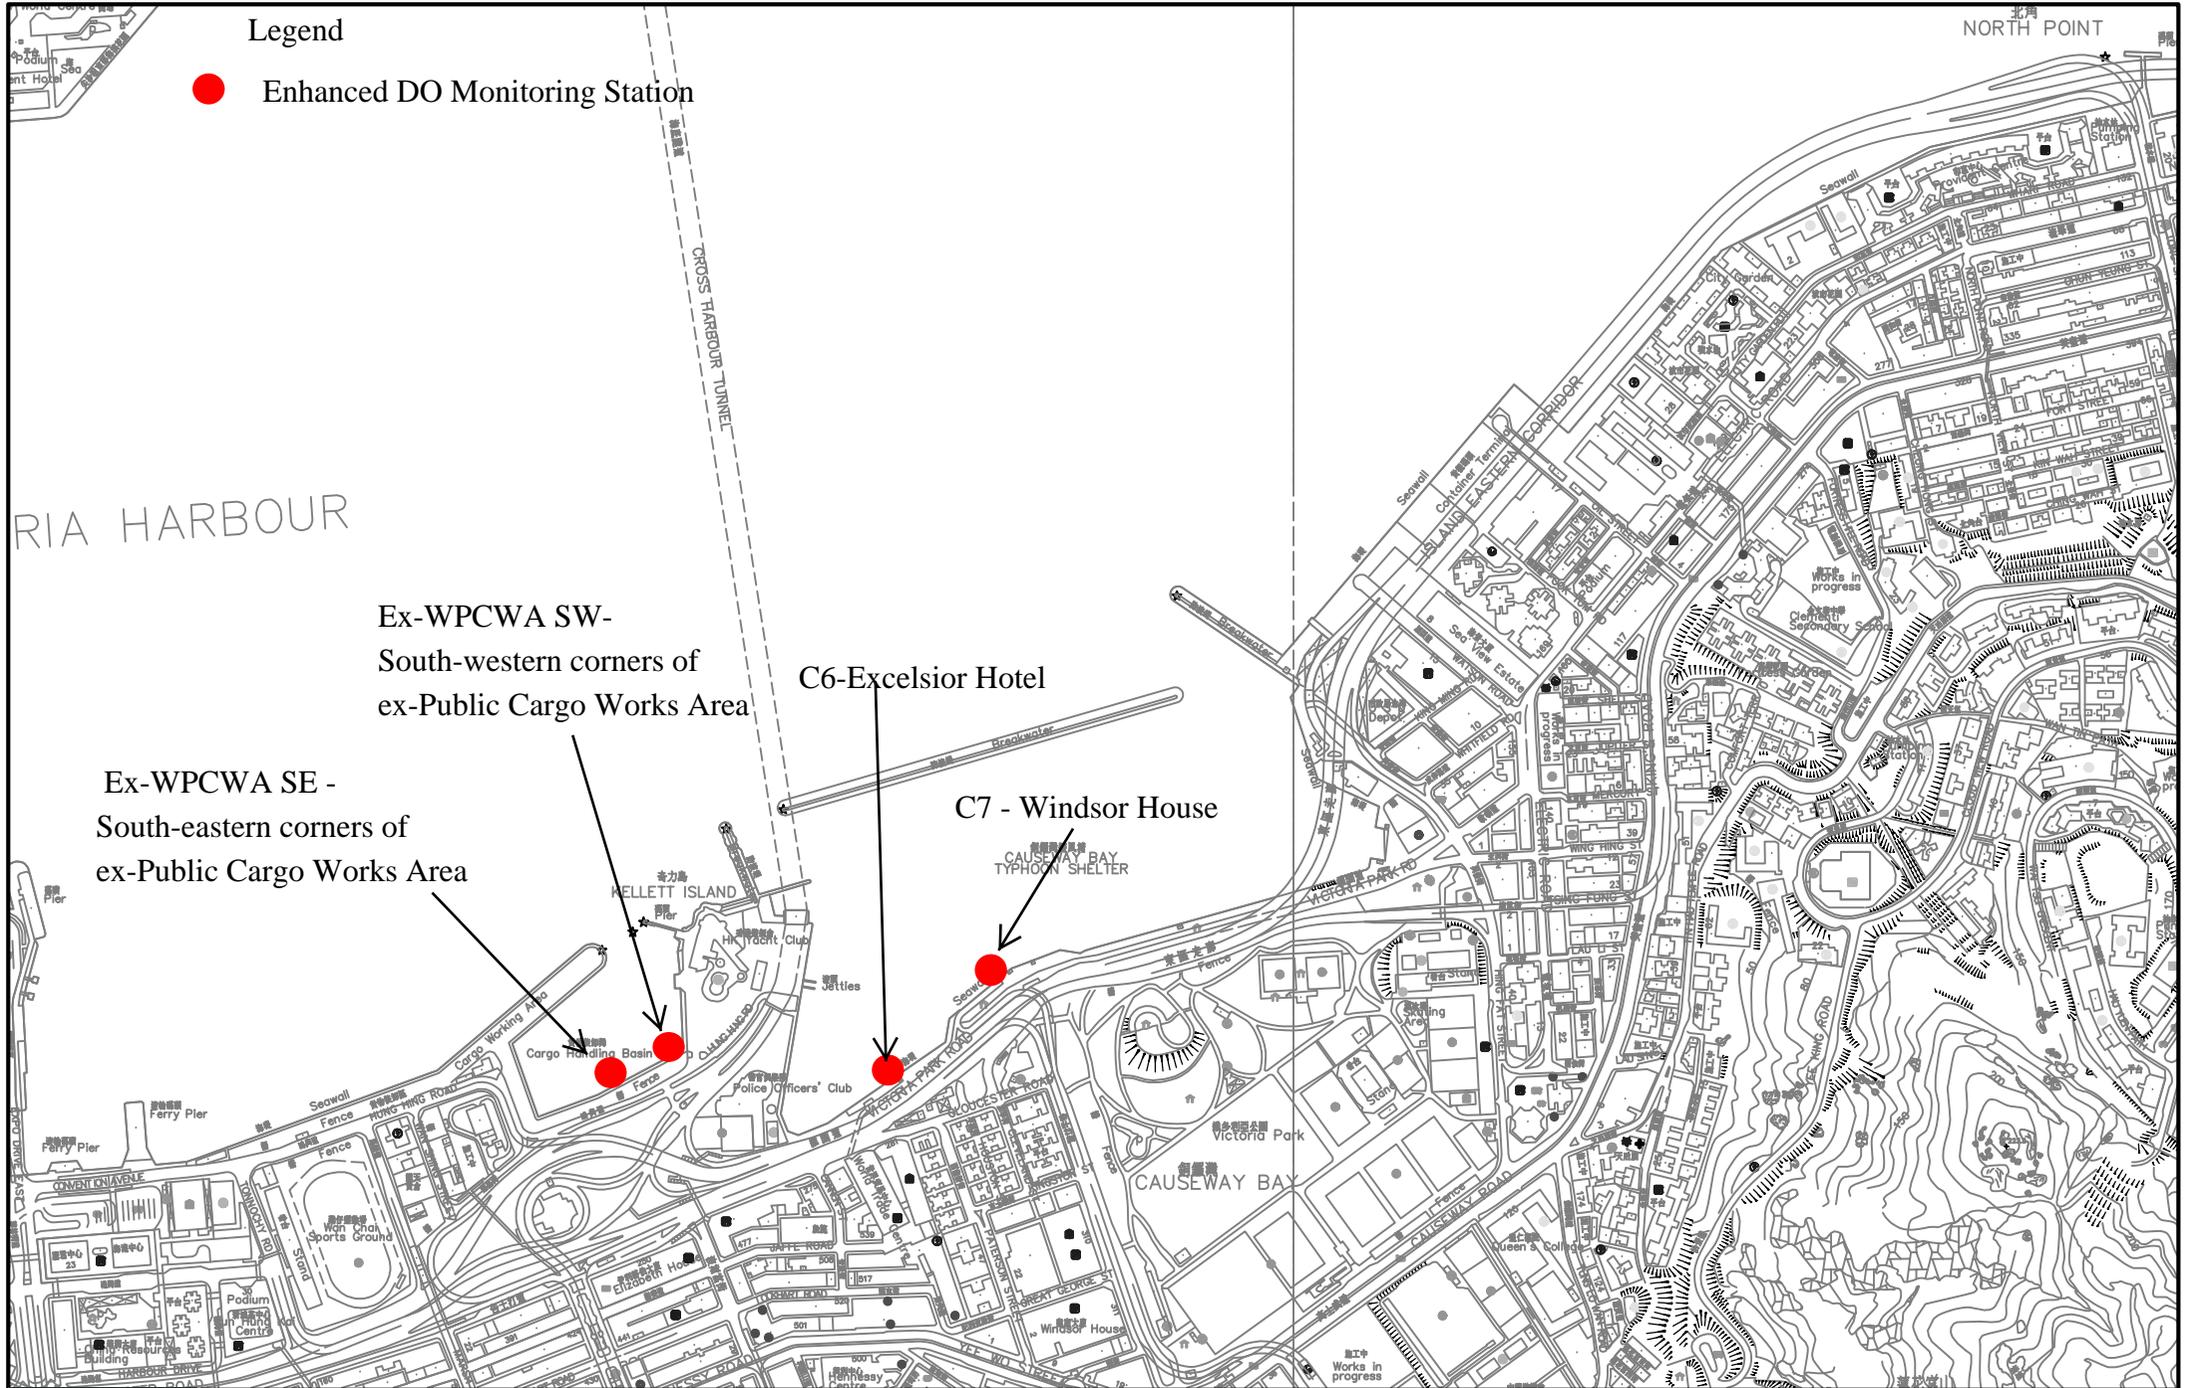

Locations of Enhance DO Monitoring Station




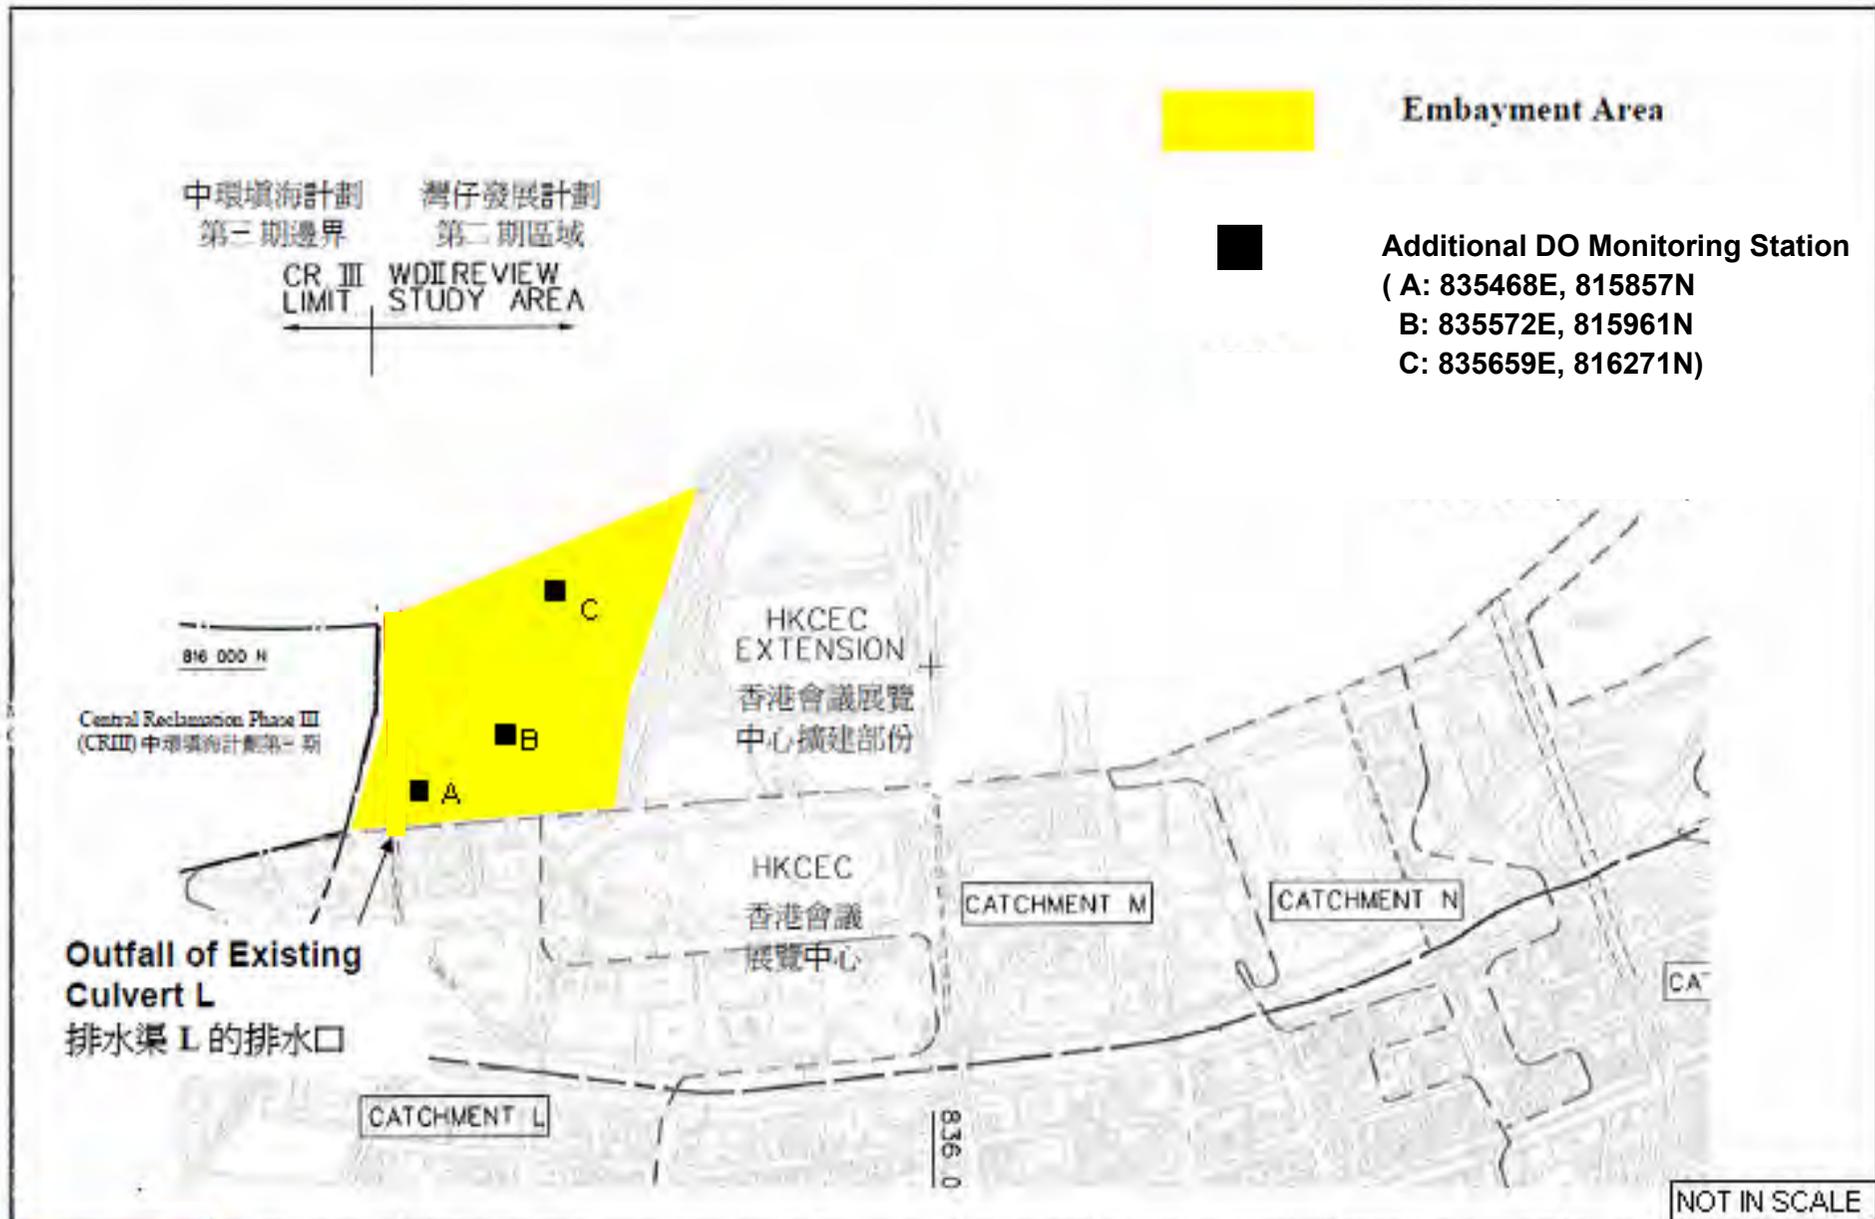

Location Plan of Additional Dissolved Oxygen Monitoring Stations for Culvert L Water Discharge Flow

**Legend**


- ◆ Water Quality Monitoring Stations
- C1 Hong Kong Convention and Exhibition Centre Extension
- C2 Telecom House/ HK Academy For Performing Art/ Shui On Centre
- C3 Hong Kong Convention and Exhibition Centre Phase 1
- C4 Wan Chai Tower and Great Eagle Centre
- C5 Sun Hung Kai Centre
- C6 Proposed Exhibition Station/ World Trade Centre
- C7 Windsor House
- C8 City Garden
- C9 Provident Centre

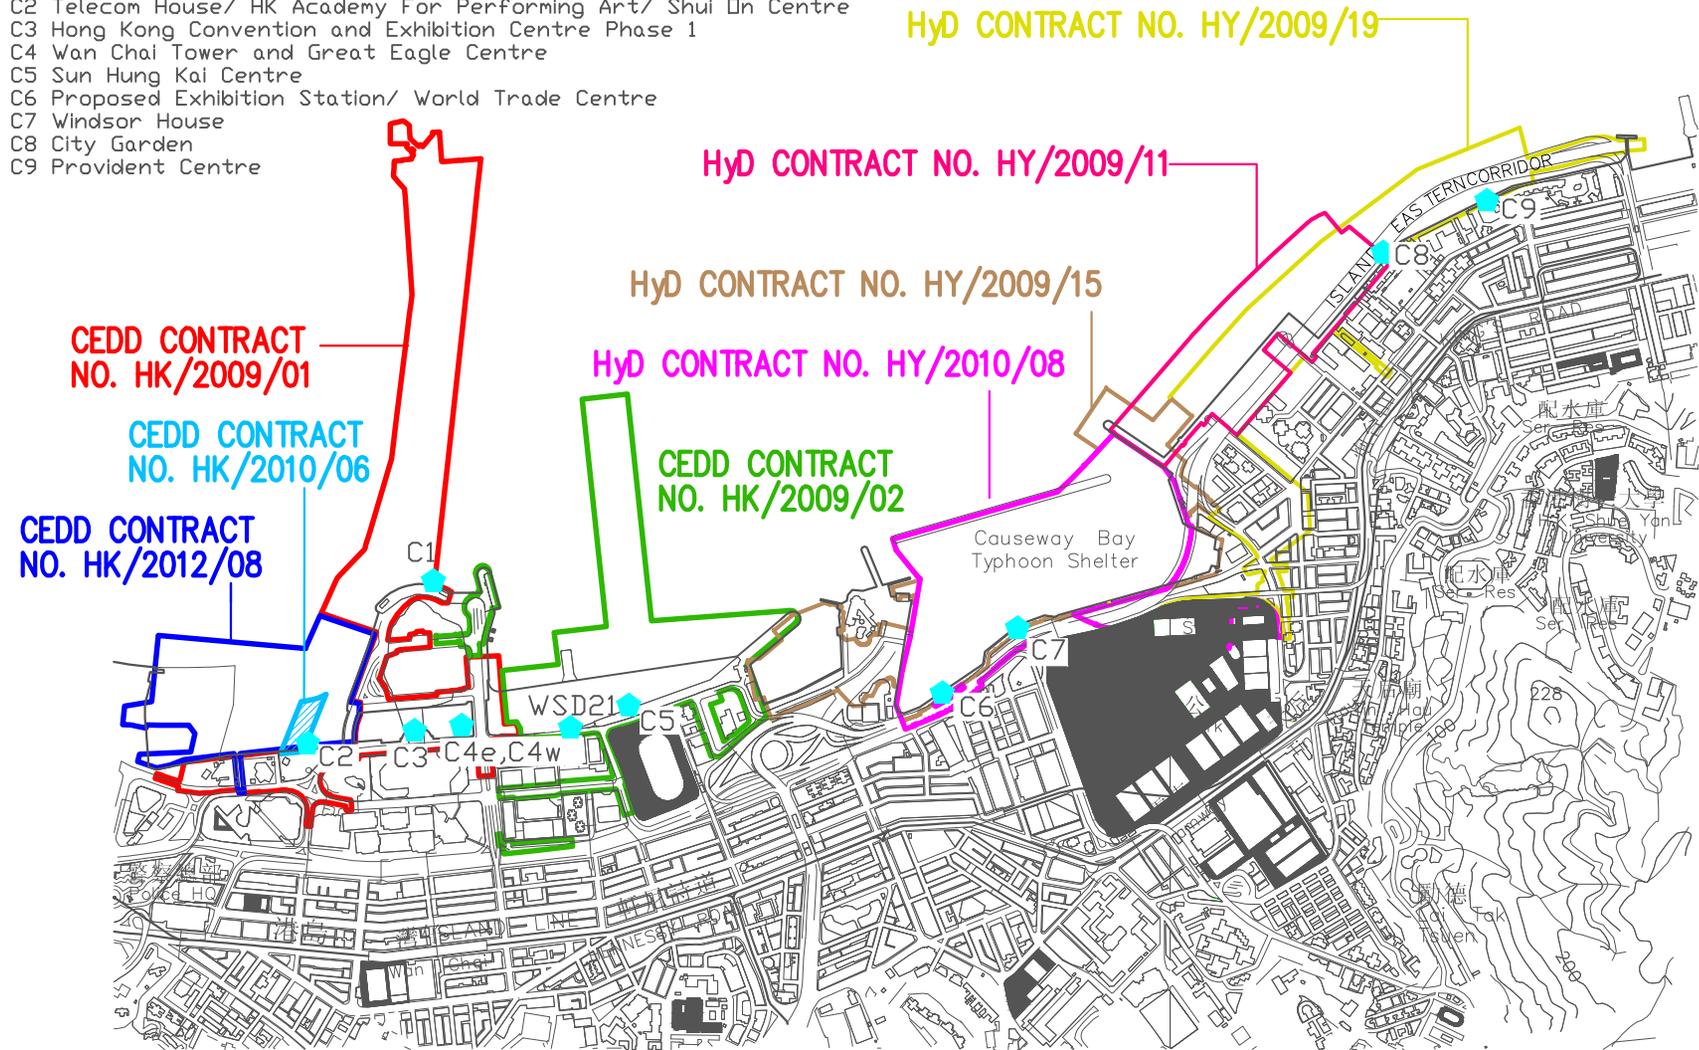


# LOCATIONS OF WATER QUALITY MONITORING STATIONS

**Legend**

- ◆ Water Quality Monitoring Stations
- RW21-P789 (Wanchai WSD intake/ Great Eagle Centre/ China Resources Centre/ Sun Hung Kai Centre)
- C1 Hong Kong Convention and Exhibition Centre Extension
- P1 Hong Kong Convention and Exhibition Centre Phase 1
- P3 HK Academy For Performing Art
- P4 Shui On Centre
- P5 Government buildings (Wanchai Tower/ Revenue Tower/ Immigration Tower)
- C6 Proposed Exhibition Station/ World Trade Centre
- C7 Windsor House

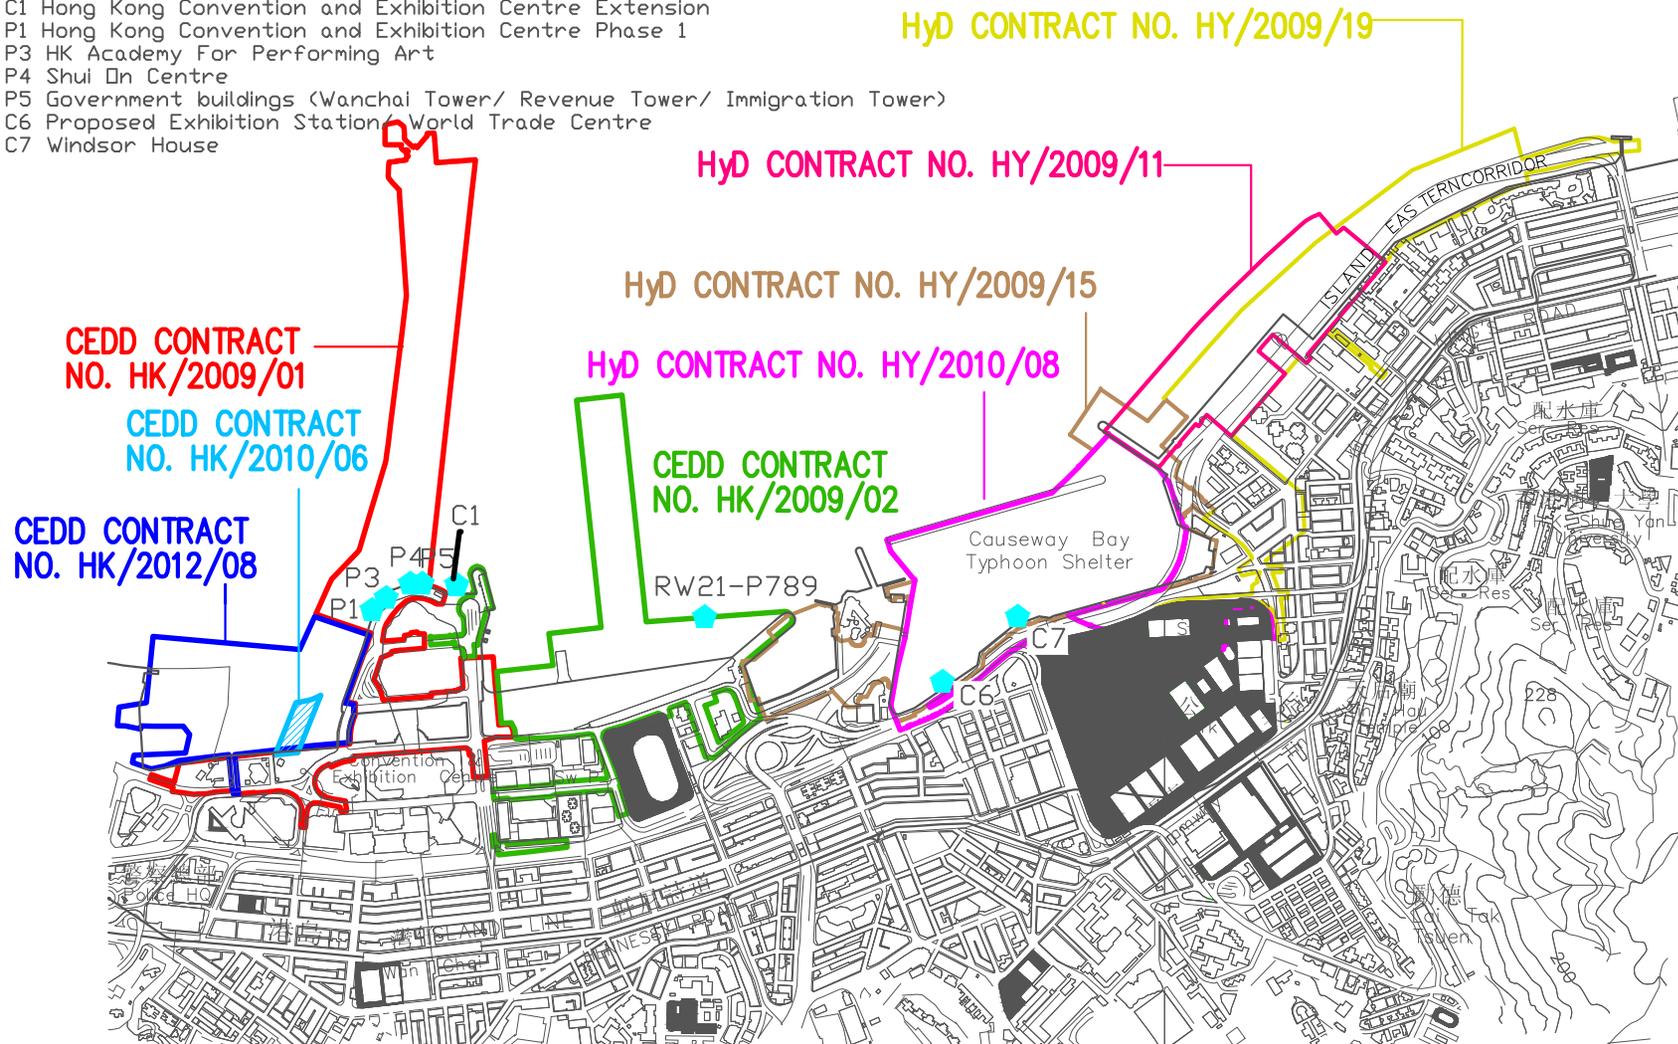

# LOCATIONS OF WATER QUALITY MONITORING STATIONS

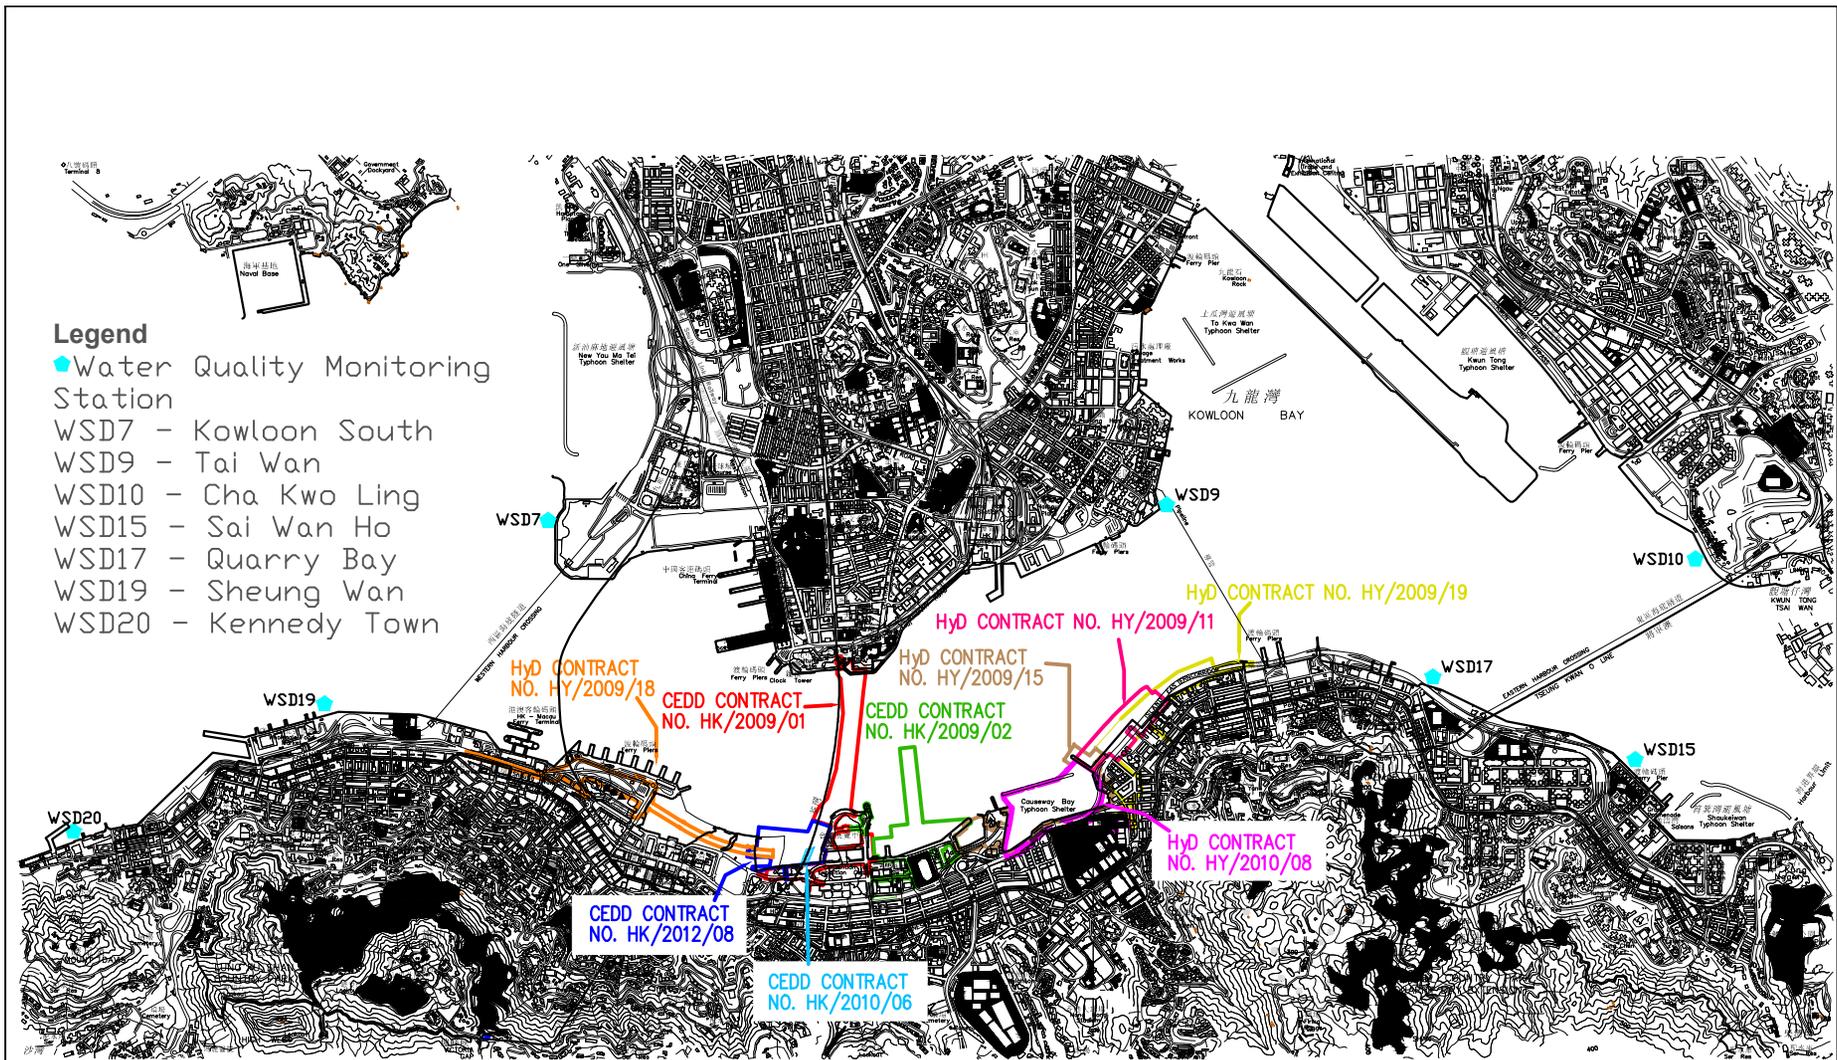

**LOCATIONS OF WATER QUALITY MONITORING STATIONS**

**Legend**

- Additional □ Monitoring Station


CEDD CONTRACT  
NO. HK/2012/08

CEDD CONTRACT  
NO. HK/2010/06

CEDD CONTRACT  
NO. HK/2009/01

CEDD CONTRACT  
NO. HK/2009/02

HyD CONTRACT  
NO. HY/2009/15

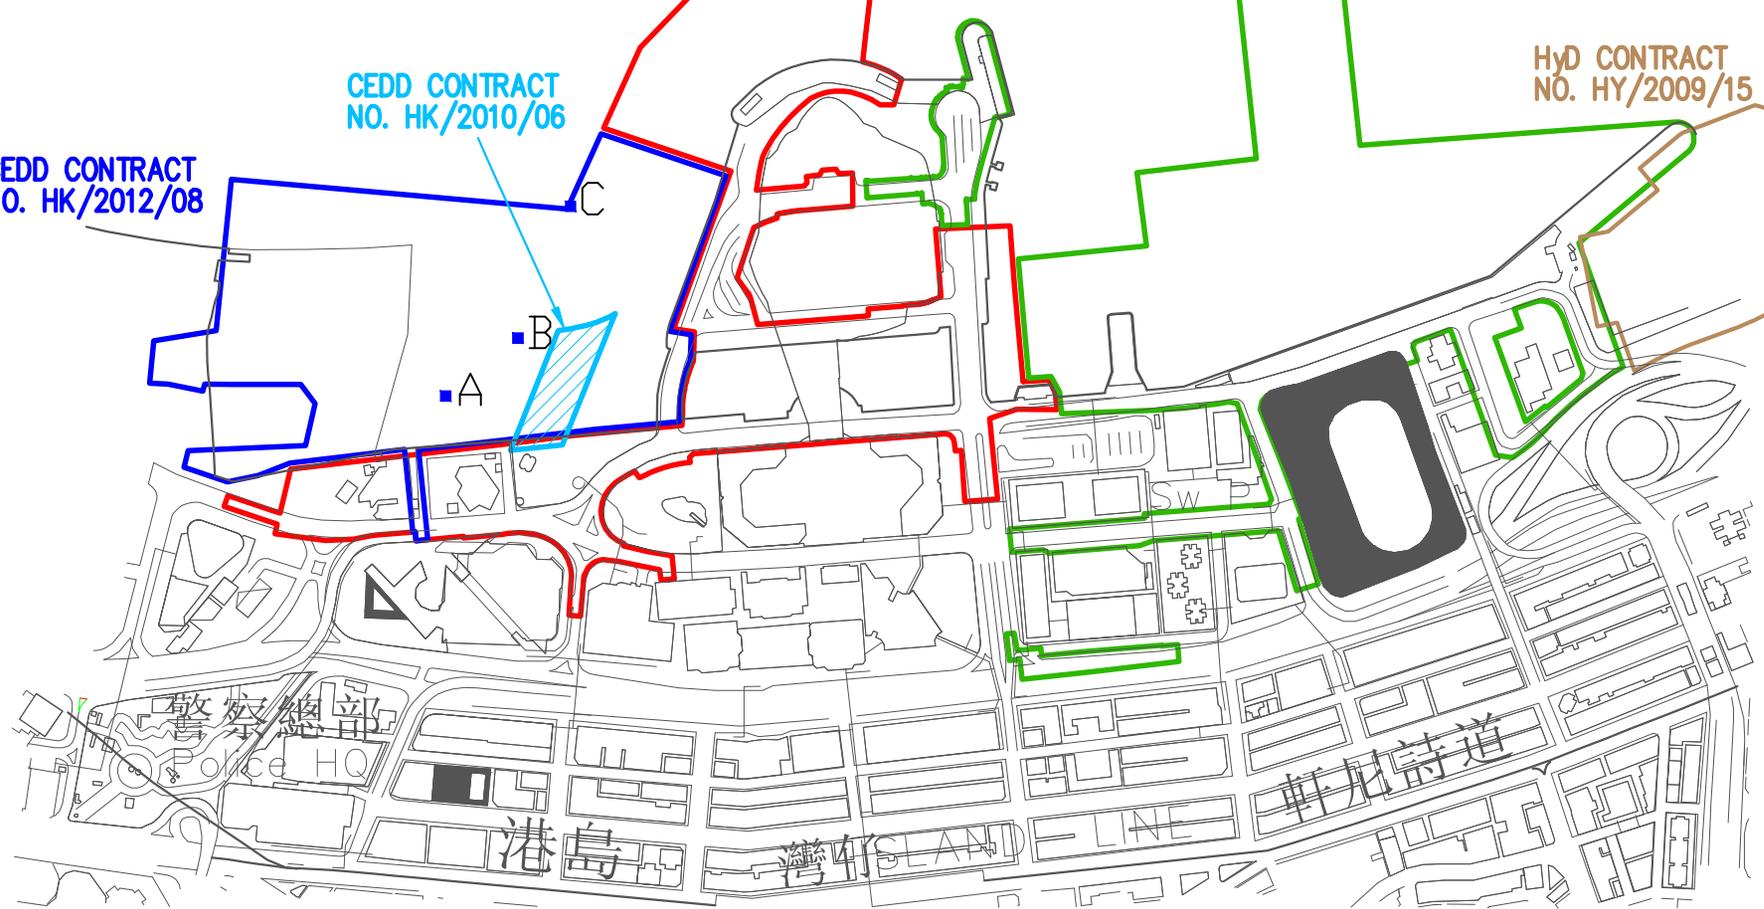

**LOCATIONS OF ADDITIONAL DISSOLVED OXYGEN MONITORING STATIONS FOR CULVERT L WATER DISCHARGE FLOW**



***Appendix 3.1***

***Environmental Mitigation Implementation Schedule***

Environmental Mitigation Implementation Schedule

Implementation Schedule for Air Quality Control

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>Construction Phase</b>								
<i>For the Whole Project</i>								
S3.6.5	Four times a day watering of the work site with active operations.	Work site / during construction	Contractor		√			EIAO-TM
S3.8.1	Implementation of dust suppression measures stipulated in Air Pollution Control (Construction Dust) Regulation. The following mitigation measures, good site practices and a comprehensive dust monitoring and audit programme are recommended to minimise cumulative dust impacts. <ul style="list-style-type: none"> <li>Strictly limit the truck speed on site to below 10 km per hour and water spraying to keep the haul roads in wet condition;</li> <li>Watering during excavation and material handling;</li> <li>Provision of vehicle wheel and body washing facilities at the exit points of the site, combined with cleaning of public roads where necessary; and</li> <li>Tarpaulin covering of all dusty vehicle loads transported to, from and between site locations.</li> </ul>	Work site / during construction	Contractor		√			

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.5.6	For the dredging activities carried out in the vicinity of Police Officers' Club, the dredging operation will be restricted to only 1 small close grab dredger to minimise the odour impact during the dredging activity. The dredging rate should be reduced as much as practicable for the area in close proximity to the Police Officers' Club. The sediments contain highly contaminated mud which may be disposed with the use of geosynthetic containers (details shall refer to Section 6), grab dredger has to be used for filling up the geosynthetic containers on barges. the dredging rate for the removal of the sediments at the south-west corner of the typhoon shelter shall be slowed down or restricted to specific non-popular hours in weekdays when it is necessary during construction.	Corner of CBTS/implementation of harbour-front enhancement	CEDD <sup>1</sup>		√			EIAO-TM
S3.8.8	Carry out dredging at the corner of CBTS to remove the sediment and clean the slime attached on the CBTS shoreline seawall	Corner of CBTS & CBTS shoreline seawall/implementation of harbour-front enhancement	CEDD <sup>2</sup>		√			EIAO-TM
<b>Operation Phase</b>								
<i>For the Whole Project</i>								

<sup>1</sup> CEDD will identify an implementation agent.

<sup>2</sup> CEDD will identify an implementation agent.

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S3.10.2	Monthly (from July to September) monitoring of odour impacts, for a period of 5 years, is proposed during the operational phase of the Project to ascertain the effectiveness of the Enhancement Package over time, and to monitor any on-going odour impacts at the ASRs.	Planned ASRs (CBTS Breakwater)/First 5-year period of operation phase	CEDD <sup>1</sup>			√		EIAO-TM
<b>For DPI – CWB (Within the Project Boundary)</b>								
S3.6.53 – S3.6.54	The design parameters of the East and Central Ventilation Buildings as set in Tables 3.10 and 3.11	East and Central Ventilation Buildings / During operation of the Trunk Road	HyD			√		
S3.10.2	Air quality monitoring for the operation performance of the East Ventilation Building and associated East Vent Shaft will be conducted.	East Vent Shaft / During operation of the East Ventilation Building and associated East Vent Shaft	HyD			√		EIAO-TM

- Des - Design, C - Construction, O – Operation, and Dec – Decommissioning

**Table A13.2 Implementation Schedule for Noise Control**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>Construction Phase</b>								
<b>For the Whole Project</b>								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S4.9.4	<p>Good Site Practice:</p> <ul style="list-style-type: none"> <li>Only well-maintained plant shall be operated on-site and plant shall be serviced regularly during the construction program.</li> <li>Silencers or mufflers on construction equipment shall be utilized and shall be properly maintained during the construction program.</li> <li>Mobile plant, if any, shall be sited as far away from NSRs as possible.</li> <li>Machines and plant (such as trucks) that may be in intermittent use shall be shut down between works periods or shall be throttled down to a minimum.</li> <li>Plant known to emit noise strongly in one direction shall, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.</li> <li>Material stockpiles and other structures shall be effectively utilized, wherever practicable, in screening noise from on-site construction activities.</li> </ul>	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
<i>For DP1 – CWB (Within the Project Boundary)</i>								

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S4.8.3 – S4.8.5	<p>Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks:</p> <ul style="list-style-type: none"> <li>Slip road 8 tunnel</li> <li>Construction of diaphragm wall and substructures of the tunnel approach ramp</li> <li>Excavation</li> <li>Construction of slabs</li> <li>Backfill</li> <li>Demolition and construction of substructures for the IEC</li> <li>Demolition works of existing piers and crossheads of the marine section of the existing IEC</li> </ul> <p>Use of PME grouping for the following tasks:</p> <ul style="list-style-type: none"> <li>At-grade road construction</li> <li>Substructure for IECL connection</li> </ul>	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
<i>For DP2 – WDII Major Roads (Road P2)</i>								
S4.8.3 – S4.8.4	<p>Use of quiet powered mechanical equipment, movable noise barrier and temporary noise barrier for the following tasks:</p> <ul style="list-style-type: none"> <li>Temporary road diversion</li> <li>Resurfacing</li> <li>At-grade roadwork</li> </ul>	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
<i>For DP3 – Reclamation Works</i>								
S4.8.3 – S4.8.4	<p>Use of quiet powered mechanical equipment for the following task:</p> <ul style="list-style-type: none"> <li>Filling behind seawall</li> <li>Seawall construction</li> </ul>	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>For DP5 – Wan Chai East Sewage Outfall</b>								
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment for the following tasks: <ul style="list-style-type: none"> <li>Submarine pipelines (marine section)</li> </ul> Use of quiet powered mechanical equipment and movable noise barrier for the following tasks: <ul style="list-style-type: none"> <li>Installation of a new pipeline (land section)</li> </ul>	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO
<b>For DP6 – Cross-Harbour Water Mains from Wan Chai to Tsim Sha Tsui</b>								
S4.8.3 – S4.8.4	Use of quiet powered mechanical equipment for the following tasks: <ul style="list-style-type: none"> <li>Submarine pipelines (marine section)</li> </ul>	Work Sites / During Construction	Contractor		√			EIAO-TM, NCO

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>Operation Phase</b>								
<b>For DP1 – CWB (Within the Project Boundary)</b>								

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S4.8.14 – S4.8.18	<ul style="list-style-type: none"> <li>For Existing NSRs</li> <li>about 235m length of noise semi-enclosure with transparent panel covering the westbound slip road from the IEC</li> <li>about 230m length of noise semi-enclosure with transparent panel covering the main carriageways (eastbound and westbound) of the CWB and IEC</li> <li>about 135m length of 5.5m high cantilevered noise barrier with 3m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC</li> <li>about 95m length of 5.5m high cantilevered noise barrier with 1m cantilever inclined at 45° with transparent panel on the eastbound slip road to the IEC</li> <li>about 350m length of 3.5m high vertical noise barrier with transparent panel on the eastbound slip road to the IEC</li> <li>low noise road surfacing for the trunk road (except tunnel section and beneath the landscaped deck at the eastern portal area) with speed limit of 70 km/hour</li> </ul> For Future/Planned NSRs	Near North Point / Before commencement of operation of road project  In between the Electric Centre (next to City Garden) and CDA(1) site / Before occupation of Planned NSRs in CDA and CDA(1) sites.	HyD	√	√	√		EIAO-TM
					√	√ <sup>#</sup>		

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> <li>The openable windows of the temple, if any, should be orientated so as to avoid direct line of sight to the existing Victoria Park Road as far as practicable.</li> </ul>	Near Causeway Bay Fire Station / During detailed design of the re-provisioned Tin Hau Temple	Project Proponent for the re-provisioned Tin Hau Temple	√				

\* Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

<sup>#</sup> Only the steel frame for this section of noise semi-enclosure would be erected in advance during the construction of the westbound slip road.

Appendix 3.1

**Table A13.3 Implementation Schedule for Water Quality Control**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>Construction Phase</b>								
<i>For DP3 – Reclamation Works, DP5 (Wan Chai East Sewage Outfall), DP6 (Cross-Harbour Water Mains from Wan Chai to Tsim Sha Tsui), DP1 – CWB (within the Project Boundary)</i>								
S5.8	A phased reclamation approach is planned for the WDII. Containment of fill within each of the reclamation phases by seawalls is proposed, with the seawall constructed first (above high water mark) with filling carried out behind the completed seawalls. Any gaps that may need to be provided for marine access will be shielded by silt curtains to control sediment plume dispersion away from the site. Filling for seawall construction should be carried out behind the silt curtain	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO
S5.8	Dredging shall be carried out by closed grab dredger for the following works: <ul style="list-style-type: none"> <li>• Seawall construction in all the reclamation areas;</li> <li>• Construction of the CWB Tunnel</li> <li>• Construction of the proposed WSD water mains; and</li> <li>• Construction of the proposed Wan Chai East sewage outfall pipelines.</li> </ul>	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO
S5.8, Figure 5.3	Dredging for the Wan Chai East sewage outfall pipelines shall not be carried out concurrently with the following activities: <ul style="list-style-type: none"> <li>• Dredging along the proposed cross-harbour water mains;</li> <li>• Dredging along the seawall in the Wan Chai Reclamation (WCR) zone (area between HKCEC Extension and PCWA).</li> </ul>	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines																								
				Des	C	O	Dec																									
S5.8	The water body behind the temporary reclamations within the Causeway Bay typhoon shelter shall not be fully enclosed.	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																								
S5.8	As a mitigation measure, to avoid the accumulation of water borne pollutants within the temporary embayment between CRIII and HKCEC1, an impermeable barrier, suspended from a floating boom on the water surface and extending down to the seabed, will be erected by the contractor before the HKCEC1 commences. The barrier will channel the stormwater discharge flows from Culvert L to the outside of the embayment. The contractor will maintain this barrier until the reclamation works in HKCEC2W are carried out and the new Culvert L extension is constructed.	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																								
S5.8, Figure 5.3	The total dredging rates in each of the marine works zones shall not be more than the maximum production rates stated in the table below. These are the production rates without considering the effect of silt curtain.	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																								
<table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th rowspan="2">Reclamation Area</th> <th colspan="2">Maximum Dredging Rate</th> <th rowspan="2">Maximum Dredging Rate (m<sup>3</sup> per week)</th> </tr> <tr> <th>m<sup>3</sup> per day</th> <th>m<sup>3</sup> per hour (for 16 hrs per day)</th> </tr> </thead> <tbody> <tr> <td colspan="4"><b>Dredging along seawall or breakwater</b></td> </tr> <tr> <td>North Point Shoreline Zone (NPR)</td> <td>6,000</td> <td>375</td> <td>42,000</td> </tr> <tr> <td>Causeway Bay</td> <td>1,500</td> <td>94</td> <td>10,500</td> </tr> <tr> <td>Shoreline Zone</td> <td>6,000</td> <td>375</td> <td>42,000</td> </tr> <tr> <td>PCWA Zone</td> <td>5,000</td> <td>313</td> <td>35,000</td> </tr> </tbody> </table>		Reclamation Area	Maximum Dredging Rate		Maximum Dredging Rate (m <sup>3</sup> per week)	m <sup>3</sup> per day	m <sup>3</sup> per hour (for 16 hrs per day)	<b>Dredging along seawall or breakwater</b>				North Point Shoreline Zone (NPR)	6,000	375	42,000	Causeway Bay	1,500	94	10,500	Shoreline Zone	6,000	375	42,000	PCWA Zone	5,000	313	35,000					
Reclamation Area	Maximum Dredging Rate		Maximum Dredging Rate (m <sup>3</sup> per week)																													
	m <sup>3</sup> per day	m <sup>3</sup> per hour (for 16 hrs per day)																														
<b>Dredging along seawall or breakwater</b>																																
North Point Shoreline Zone (NPR)	6,000	375	42,000																													
Causeway Bay	1,500	94	10,500																													
Shoreline Zone	6,000	375	42,000																													
PCWA Zone	5,000	313	35,000																													

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures				Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines																						
							Des	C	O	Dec																							
	<table border="1"> <tr> <td>Wan Chai Shoreline Zone (WCR)</td> <td>6,000</td> <td>375</td> <td>42,000</td> </tr> <tr> <td>HKCEC Shoreline Zone (HKCEC)</td> <td>1,500</td> <td>94</td> <td>10,500</td> </tr> <tr> <td>HKCEC Stage 1 &amp; 3</td> <td>6,000</td> <td>375</td> <td>42,000</td> </tr> <tr> <td>HKCEC Stage 2</td> <td>1,500</td> <td>94</td> <td>10,500</td> </tr> <tr> <td>Cross Harbour Water Mains</td> <td>1,500</td> <td>94</td> <td>10,500</td> </tr> <tr> <td>Wan Chai East Submarine Sewage Pipeline</td> <td>1,500</td> <td>94</td> <td>10,500</td> </tr> </table> <p>Note: 1,500 m<sup>3</sup> per day shall be applied for construction of the western seawall of WCR1.</p>	Wan Chai Shoreline Zone (WCR)	6,000	375	42,000	HKCEC Shoreline Zone (HKCEC)	1,500	94	10,500	HKCEC Stage 1 & 3	6,000	375	42,000	HKCEC Stage 2	1,500	94	10,500	Cross Harbour Water Mains	1,500	94	10,500	Wan Chai East Submarine Sewage Pipeline	1,500	94	10,500								
Wan Chai Shoreline Zone (WCR)	6,000	375	42,000																														
HKCEC Shoreline Zone (HKCEC)	1,500	94	10,500																														
HKCEC Stage 1 & 3	6,000	375	42,000																														
HKCEC Stage 2	1,500	94	10,500																														
Cross Harbour Water Mains	1,500	94	10,500																														
Wan Chai East Submarine Sewage Pipeline	1,500	94	10,500																														
S5.8, Figure 5.3	Dredging along the seawall at WCR1 shall be undertaken initially at 1,500m <sup>3</sup> per day for construction of the western seawall (which is in close proximity of the WSD intake), followed by partial seawall construction at the western seawall (above high water mark) to protect the adjacent intakes as much as possible from further dredging activities.				Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																						
S5.8, Figure 5.3	For dredging within the Causeway Bay typhoon shelter, seawall shall be partially constructed to protect the nearby seawater intakes from further dredging activities. For example, at TCBR1W, the southern and eastern seawalls shall be constructed first (above high water mark) so that the seawater intakes at the inner water would be protected from the impacts from the remaining dredging activities along the northern boundary.				Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																						
S5.8, Figure 5.3	Silt curtains shall be deployed around the closed grab dredgers during seawall dredging and seawall trench filling in the areas of HKCEC, WCR, TCBR and NP.				Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																						
S5.8, Figure 5.3	Silt screens shall be applied to seawater intakes at interim construction stages as stated below:				Work site / During the construction period	Contractor		√			EIAO-TM, WPCO																						
	<table border="1"> <thead> <tr> <th>Interim Construction Stage</th> <th>Location of Applications</th> </tr> </thead> <tbody> <tr> <td>Scenario 2A in early 2009 with concurrent dredging activities at HKCEC, WCR, TPCWA,</td> <td>WSD saltwater intakes at Sai Wan Ho, Quarry Bay, Sheung Wan, Wan Chai, Kowloon South Cooling water intakes for Hong Kong Convention and Exhibition Centre Extension, Hong Kong</td> </tr> </tbody> </table>	Interim Construction Stage	Location of Applications	Scenario 2A in early 2009 with concurrent dredging activities at HKCEC, WCR, TPCWA,	WSD saltwater intakes at Sai Wan Ho, Quarry Bay, Sheung Wan, Wan Chai, Kowloon South Cooling water intakes for Hong Kong Convention and Exhibition Centre Extension, Hong Kong																												
Interim Construction Stage	Location of Applications																																
Scenario 2A in early 2009 with concurrent dredging activities at HKCEC, WCR, TPCWA,	WSD saltwater intakes at Sai Wan Ho, Quarry Bay, Sheung Wan, Wan Chai, Kowloon South Cooling water intakes for Hong Kong Convention and Exhibition Centre Extension, Hong Kong																																

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures		Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines						
					Des	C	O	Dec							
	<table border="1"> <tr> <td>TBW, NP and Water Mains Zone</td> <td>Convention and Exhibition Centre Phase I, Telecom House / HK Academy for Performing Arts / Shun On Centre, Wan Chai Tower / Revenue Tower / Immigration Tower and Sun Hung Kai Centre</td> </tr> <tr> <td>Scenario 2B in late 2009/2010 with concurrent dredging activities at Sewage Pipelines Zone and TCBR.</td> <td>WSD saltwater intakes at Sheung Wan, Wan Chai Cooling water intakes for Queensway Government Offices, Excelsior Hotel, World Trade Centre and Windsor House.</td> </tr> <tr> <td>Scenario 2C in 2011 with concurrent dredging activities at HKCEC and TCBR.</td> <td>WSD saltwater intakes at Sheung Wan and Re-provisioned WSD Wan Chai saltwater intake. Cooling water intakes for MTR South, Excelsior Hotel &amp; World Trade Centre and re-provisioned Windsor House.</td> </tr> </table>	TBW, NP and Water Mains Zone	Convention and Exhibition Centre Phase I, Telecom House / HK Academy for Performing Arts / Shun On Centre, Wan Chai Tower / Revenue Tower / Immigration Tower and Sun Hung Kai Centre	Scenario 2B in late 2009/2010 with concurrent dredging activities at Sewage Pipelines Zone and TCBR.	WSD saltwater intakes at Sheung Wan, Wan Chai Cooling water intakes for Queensway Government Offices, Excelsior Hotel, World Trade Centre and Windsor House.	Scenario 2C in 2011 with concurrent dredging activities at HKCEC and TCBR.	WSD saltwater intakes at Sheung Wan and Re-provisioned WSD Wan Chai saltwater intake. Cooling water intakes for MTR South, Excelsior Hotel & World Trade Centre and re-provisioned Windsor House.								
TBW, NP and Water Mains Zone	Convention and Exhibition Centre Phase I, Telecom House / HK Academy for Performing Arts / Shun On Centre, Wan Chai Tower / Revenue Tower / Immigration Tower and Sun Hung Kai Centre														
Scenario 2B in late 2009/2010 with concurrent dredging activities at Sewage Pipelines Zone and TCBR.	WSD saltwater intakes at Sheung Wan, Wan Chai Cooling water intakes for Queensway Government Offices, Excelsior Hotel, World Trade Centre and Windsor House.														
Scenario 2C in 2011 with concurrent dredging activities at HKCEC and TCBR.	WSD saltwater intakes at Sheung Wan and Re-provisioned WSD Wan Chai saltwater intake. Cooling water intakes for MTR South, Excelsior Hotel & World Trade Centre and re-provisioned Windsor House.														
S5.8	<p>Other mitigation measures include:</p> <ul style="list-style-type: none"> <li>mechanical grabs, if used, shall be designed and maintained to avoid spillage and sealed tightly while being lifted. For dredging of any contaminated mud, closed watertight grabs must be used;</li> <li>all vessels shall be sized so that adequate clearance is maintained between vessels and the seabed in all tide conditions, to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;</li> <li>all hopper barges and dredgers shall be fitted with tight fitting seals to their bottom openings to prevent leakage of material;</li> <li>construction activities shall not cause foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site or dumping grounds;</li> <li>loading of barges and hoppers shall be controlled to prevent splashing of dredged material into the surrounding water. Barges or hoppers shall not be filled to a level that will cause the overflow of materials or polluted water during loading or transportation; and</li> </ul>		Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO (TM-DSS)						

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> <li>before commencement of the reclamation works, the holder of Environmental Permit has to submit plans showing the phased construction of the reclamation, design and operation of the silt curtain.</li> </ul>							
S5.8	<p>Silt screens are recommended to be deployed at the seawater intakes during the reclamation works period. Installation of silt screens at the seawater intake points may cause a potential for accumulation and trapping of pollutants, floating debris and refuse behind the silt screens and may lead to potential water quality deterioration at the seawater intake points. Major sources of pollutants and floating refuse include the runoff and storm water discharges from the nearby coastal areas. As a mitigation measure to avoid the pollutant and refuse entrapment problems and to ensure that the impact monitoring results are representative, regular maintenance of the silt screens and refuse collection shall be performed at the monitoring stations at regular intervals on a daily basis. The Contractor shall be responsible for keeping the water behind the silt screen free from floating rubbish and debris during the impact monitoring period.</p>	Work site / During the construction period	Contractor		√			EIAO-TM, WPCO

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S5.8	<p>Dredging of contaminated mud is recommended as a mitigation measures for control of operational odour impact from the Causeway Bay typhoon shelter. In recognition of the potential impacts caused by dredging activities close to the seawater intakes, only 1 small close grab dredger shall be operated within the typhoon shelter (for the dredging to mitigate odour impact) at any time to minimize the potential impact. Double silt curtains shall be deployed to fully enclose the closed grab dredger during the dredging operation. In addition, an impermeable barrier, suspended from a floating boom on the water surface and extended down to the seabed, shall be erected to isolate the adjacent intakes as much as possible from dredging activities. For example, if dredging is to be carried out at the southwest corner of the typhoon shelter, physical barriers shall be erected to west of the cooling water intake for Excelsior Hotel so that the intake would be shielded from most of the SS generated from the dredging operation to the west of the intake. For area in close proximity of the cooling water intake point, the dredging rate shall be reduced as much as practicable. Site audit and water quality monitoring shall be carried out at the seawater intakes during the dredging operations. Daily monitoring of SS at the cooling water intake shall be carried out, and 24 hour monitoring of turbidity at the intakes shall be implemented during the dredging activities. If the monitoring results indicate that the dredging operation has caused significant changes in water quality conditions at the seawater intakes, appropriate actions shall be taken to stop the dredging and mitigation measures such as slowing down the dredging rate shall be implemented.</p>	Causeway Bay typhoon shelter/Implementation of harbour-front enhancement.	CEDD <sup>3</sup>		√			WPCO

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines	
				Des	C	O	Dec		
<b>For the Whole Project</b>									
S5.8	<ul style="list-style-type: none"> <li>Construction Runoff and Drainage</li> <li>use of sediment traps, wheel washing facilities for vehicles leaving the site, and adequate maintenance of drainage systems to prevent flooding and overflow;</li> <li>Permanent drainage channels shall incorporate sediment basins or traps and baffles to enhance deposition rates. The design of efficient silt removal facilities shall be based on the guidelines in Appendix A1 of ProPECC PN 1/94;</li> <li>a sediment tank constructed from pre-formed individual cells of approximately 6 - 8 m3 capacity can be used for settling ground water prior to disposal;</li> <li>oil interceptors shall be provided in the drainage system for the tunnels and regularly cleaned to prevent the release of oils and grease into the storm water drainage system after accidental spillages. The interceptor shall have a bypass to prevent flushing during periods of heavy rain;</li> <li>precautions and actions to be taken when a rainstorm is imminent or forecast, and during or after rainstorms. Particular attention shall be paid to the control of any silty surface runoff during storm events;</li> <li>on-site drainage system shall be installed prior to the commencement of other construction activities. Sediment traps shall be installed in order to minimise the sediment loading of the effluent prior to discharge;</li> <li>All temporary and permanent drainage pipes and culverts provided to facilitate runoff discharge shall be adequately designed for the controlled release of storm flows. All sediment control measures shall be regularly inspected and maintained to ensure proper and efficient operation at all times and particularly following rain storms. The temporarily diverted drainage shall be reinstated to its original condition when the construction work is finished or the temporary diversion is no longer</li> </ul>	<ul style="list-style-type: none"> <li>Work site / During the construction period</li> </ul>	Contractor		√				ProPECC PN 1/94; WPCO (TM-DSS)

<sup>3</sup> CEDD will identify an implementation agent.

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p>required.</p> <ul style="list-style-type: none"> <li>All fuel tanks and store areas shall be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity.</li> </ul>							
	<ul style="list-style-type: none"> <li>Minimum distances of 100 m shall be maintained between the storm water discharges and the existing or planned WSD flushing water intakes during construction phase.</li> </ul>							
S5.8	<p><i>Sewage from Construction Work Force</i></p> <p>Construction work force sewage discharges on site shall be connected to the existing trunk sewer or sewage treatment facilities. The construction sewage shall be handled by portable chemical toilets prior to the commission of the on-site sewer system. Appropriate numbers of portable toilets shall be provided by a licensed contractor to serve the large number of construction workers over the construction site. The Contractor shall also be responsible for waste disposal and maintenance practices.</p>	Work site / During the construction period	Contractor		√			ProPECC PN 1/94; WPCO (TM-DSS)
S5.8	<p><i>Floating Debris and Refuse</i></p> <p>Collection and removal of floating refuse shall be performed at regular intervals on a daily basis. The contractor shall be responsible for keeping the water within the site boundary and the neighbouring water free from rubbish.</p>	Work site and adjacent water / During the construction period.	Contractor		√			WPCO

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S5.8	<p><i>Storm Water Discharges</i></p> <p>Minimum distances of 100 m shall be maintained between the existing or planned stormwater discharges and the existing or planned WSD flushing water intakes.</p>	Work site and adjacent water / During the design and construction period.	Contractor	√	√			WPCO
<b>Operation Phase</b>								
<i>DPI – CWB (within the Project Boundary)</i>								
S5.8	<p>For the operation of CWB, a surface water drainage system would be provided to collect road runoff. The following operation stage mitigation measures are recommended to ensure road runoff would comply with the TM under the WPCO:</p> <ul style="list-style-type: none"> <li>The drainage from tunnel sections shall be directed through petrol interceptors to remove oil and grease before being discharged to the nearby foul water manholes.</li> <li>Petrol interceptors shall be regularly cleaned and maintained in good working condition.</li> <li>Oily contents of the petrol interceptors shall be properly handled and disposed of, in compliance with the requirements of the Waste Disposal Ordinance.</li> <li>Sewage arising from ancillary facilities of CWB (for examples, car park,</li> </ul>	CWB/During design and operational period	HyD/TD <sup>3</sup>	√		√		WPCO

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p>control room, ventilation and administration buildings and tunnel portals) shall be connected to public sewerage system. Sufficient capacity in public sewerage shall be made available to the proposed facilities.</p> <ul style="list-style-type: none"> <li>Road drainage shall also be provided with adequately designed silt trap to minimize discharge of silty runoff.</li> <li>The design of the operational stage mitigation measures for CWB shall take into account the guidelines published in ProPECC PN 5/93 "Drainage Plans subject to Comment by the EPD." All operational discharges from the CWB into drainage or sewerage systems are required to be licensed by EPD under the WPCO.</li> </ul>							

\* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

<sup>3</sup> if employ Management, Operation and Maintenance (MOM) Contract

Appendix 3.1

**Table A13.4 Implementation Schedule for Waste Management**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>Construction Phase</b>								
<i>For DP3 – Reclamation Works</i>								
	<b>Marine Sediments</b>							
S6.7.2	The dredged marine sediments would be loaded onto barges, transported to and disposed of at the designated disposal sites at South of Cheung Chau, East of Ninepin, East of Tung Lung Chau, South of Tsing Yi or East of Sha Chau to be allocated by the MFC depending on their level of contamination or at other disposal sites after consultation with the MFC and EPD. In accordance with the ETWB TCW No. 34/2002, the contaminated material must be dredged and transported with great care. The mitigation measures recommended in Section 5 of the EIA Report shall be incorporated. The dredged contaminated sediment must be effectively isolated from the environment upon final disposal and shall be disposed of at the Type 2 confined marine disposal contaminated mud pit.	Work site / During the construction period	Contractor		√			ETWB TCW No. 34/2002
S6.7.3	Based on the biological screening results, the Category H (>10xLCEL) sediment which failed the biological testing would require Type 3 special disposal. The volume of Category H sediment from the Causeway Bay typhoon shelter which would require special disposal arrangements is estimated to be approximately 0.05 Mm <sup>3</sup> . A feasible containment method is proposed whereby the dredged sediments are sealed in geosynthetic containers and, at the disposal site, the containers would be dropped into the designated contaminated mud pit where they would be covered by further mud disposal and later by the mud pit capping, thereby meeting the requirements for fully confined mud disposal.							

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.5	It will be the responsibility of the Contractor to satisfy the appropriate authorities that the contamination levels of the marine sediment to be dredged have been analysed and recorded. According to the ETWB TCW No. 34/2002, this will involve the submission of a formal Sediment Quality Report to the DEP, at least 3 months prior to the dredging contract being tendered							
S6.7.6	During transportation and disposal of the dredged marine sediments requiring Type 1 and Type 2 disposal, the following measures shall be taken to minimise potential impacts on water quality: <ul style="list-style-type: none"> <li>Bottom opening of barges shall be fitted with tight fitting seals to prevent leakage of material. Excess material shall be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.</li> </ul>							

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<ul style="list-style-type: none"> <li>Monitoring of the barge loading shall be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels shall be equipped with automatic self-monitoring devices as specified by the DEP.</li> <li>Barges or hopper barges shall not be filled to a level that would cause the overflow of materials or sediment laden water during loading or transportation.</li> </ul>							
S6.6.12	<p><b>Floating Refuse</b></p> <p>During the construction phase, the project proponent's contractor will be responsible for the collection of any refuse within their works area. Floating booms will be provided on the water surface to confine the refuse from the working barges as well as to avoid the accumulation of pollutants within temporary embayment as mentioned in Table 13.3.</p>	Work site / During the construction period	Contractor		√			
<b>For the Whole Project</b>								

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.7	<p><b>Good Site Practices</b></p> <p>Recommendations for good site practices during the construction activities include:</p> <ul style="list-style-type: none"> <li>nomination of an approved person, such as a site manager, to be responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site;</li> <li>training of site personnel in proper waste management and chemical waste handling procedures;</li> <li>provision of sufficient waste disposal points and regular collection for disposal;</li> <li>appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;</li> <li>regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors; and</li> <li>a recording system for the amount of wastes generated, recycled and disposed of (including the disposal sites).</li> </ul>	Work site / During the construction period	Contractor		√			Waste Disposal Ordinance (Cap.354)

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.8	<p><i>Waste Reduction Measures</i></p> <p>Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:</p> <ul style="list-style-type: none"> <li>segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;</li> <li>to encourage collection of aluminium cans, PET bottles and paper, separate labelled bins shall be provided to segregate these wastes from other general refuse generated by the work force;</li> <li>any unused chemicals or those with remaining functional capacity shall be recycled;</li> <li>use of reusable non-timber formwork, such as in casting the tunnel box sections, to reduce the amount of C&amp;D material.</li> <li>prior to disposal of C&amp;D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill;</li> <li>proper storage and site practices to minimise the potential for damage or contamination of construction materials; and</li> <li>plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.</li> </ul>	Work site / During planning and design stage, and construction stage	Contractor	√	√			

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.10	<p><i>General Refuse</i></p> <p>General refuse shall be stored in enclosed bins or compaction units separate from C&amp;D material. A licensed waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&amp;D material.</p> <p>A collection area shall be provided where wastes can be stored and loaded prior to removal from site. An enclosed and covered area is recommended to reduce the occurrence of 'wind blow' light material.</p>	Work site / During the construction period	Contractor		√			Public Health and Municipal Services Ordinance (Cap. 132)
S6.7.11	<p><i>Chemical Wastes</i></p> <p>After use, chemical wastes (for example, cleaning fluids, solvents, lubrication oil and fuel) shall be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Spent chemicals shall be collected by a licensed collector for disposal at the CWTF or other licensed facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.</p>	Work site / During the construction period	Contractor		√			Waste Disposal (Chemical Waste) (General) Regulation  Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes
S6.7.12	<p><i>Construction and Demolition Material</i></p> <p>C&amp;D material shall be sorted on-site into inert C&amp;D material (that is, public fill) and C&amp;D waste. All the suitable inert C&amp;D material shall be broken down to 250 mm in size for reuse as public fill in the WDII reclamation. C&amp;D waste, such as wood, glass, plastic, steel and other metals shall be reused or recycled and, as a last resort, disposed of to landfill. A suitable area shall be designated to facilitate the sorting process and a temporary stockpiling area will be required for the separated materials.</p>	Work site / During the construction period	Contractor		√			ETWB TCW No. 33/2002, 31/2004, 19/2005

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S6.7.13	In order to monitor the disposal of public fill and C&D waste at public filling facilities and landfills, respectively, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements and implemented by the Environmental Team undertaking the environmental monitoring and audit work. An Independent Environment Checker shall be responsible for auditing the results of the system.	Work site / During the construction period	Contractor and Independent Environmental Checker		√			ETWB TCW No. 31/2004
S6.7.14	<p><i>Bentonite Slurry</i></p> <p>The disposal of residual used bentonite slurry shall follow the good practice guidelines stated in ProPECC PN 1/94 "Construction Site Drainage" and listed as follows:</p> <ul style="list-style-type: none"> <li>If the disposal of a certain residual quantity cannot be avoided, the used slurry may be disposed of at the marine spoil grounds subject to obtaining a marine dumping licence from EPD on a case-by-case basis.</li> <li>If the used bentonite slurry is intended to be disposed of through the public drainage system, it shall be treated to the respective effluent standards applicable to foul sewers, storm drains or the receiving waters as set out in the Technical Memorandum of Standards for Effluents Discharged into Drainage and Sewerage Systems, Inland and Coastal Waters.</li> <li>If the used bentonite slurry is intended to be disposed to public fill reception facilities, it will be mixed with dry soil on site before disposal.</li> </ul>	Work site / During the construction period	Contractor		√			ProPECC PN 1/94

\* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Appendix 3.1

Table A13.5 Implementation Schedule for Land Contamination

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>Construction Phase</b>								
<i>For the Whole Project</i>								
S.12.6	<ul style="list-style-type: none"> <li>The contaminated site shall be cleaned up before commencement of site clearance and construction work at the concerned area which may disturb the ground.</li> </ul>	A King Marine / Before commencement of construction activities at A King Marine.	Project proponent for the re-provisioned Tin Hau Temple	√				<p>"Guidance Notes for Investigation and Remediation of Contaminated Sites of Petrol Filling Stations, Boatyards, and Car Repair/Dismantling Workshops" published by EPD, HKSAR</p> <p>EPD ProPECC Note No. 3/94</p>
S7.10	<p>During soil remediation works, the Contractor for the excavation works shall take note of the following points for excavation:</p> <ul style="list-style-type: none"> <li>Excavation profiles must be properly designed and executed;</li> <li>In case the soil to be excavated is situated beneath the groundwater table, it may be necessary to lower the groundwater table by installing well points or similar means;</li> <li>Quantities of soil to be excavated must be estimated;</li> <li>It maybe necessary to split quantities of soil according to soil type, degree and nature of contamination.</li> <li>Temporary storage of soil at intermediate depot or on-site</li> </ul>	A King Marine / During soil remediation works	Contractor	√				<p>Air Pollution Control Ordinance</p> <p>Noise Control Ordinance</p> <p>Waste Disposal Ordinance</p> <p>Waste Disposal (Chemical Waste) (General) Regulation</p>

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	maybe required. The storage site shall include protection facilities for leaching into the ground. eg. Liner maybe required.							
	<ul style="list-style-type: none"> <li>Supply of suitable clean backfill materials is needed after excavation.</li> <li>Care must be taken of existing buildings and utilities.</li> <li>Precautions must be taken to control of ground settlement</li> <li>Speed controls for vehicles shall be imposed on dusty site areas.</li> <li>Vehicle wheel and body washing facilities at the site's exit points shall be established and used.</li> </ul> <p>The following environmental mitigation measures shall be strictly followed during the operation and/or maintenance of the CS/S facilities:</p>							Water Pollution Control Ordinance

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p><u>Air Quality Mitigation Measures</u></p> <ul style="list-style-type: none"> <li>The loading, unloading, handling, transfer or storage of cement shall be carried out in an enclosed system.</li> <li>The loading, unloading, handling, transfer or storage of other materials which may generate airborne dust emissions such as untreated soil and oversize materials sorted out from the screening plant and stabilized soil stockpiled in the designated handling area, shall be carried out in such a manner to prevent or minimise dust emissions. These materials shall be adequately wetted prior to and during the loading, unloading and handling operations.</li> <li>All practicable measures, including speed controls for vehicles, shall be taken to prevent or minimize the dust emission caused by vehicle movement.</li> <li>Tarpaulin or low permeable sheet shall be put on dusty vehicle loads transported between site locations.</li> </ul>							
	<p><u>Noise Mitigation Measures</u></p> <ul style="list-style-type: none"> <li>The mixing facilities shall be sited as far as practicable to the nearby noise sensitive receivers.</li> <li>Simultaneous operation of mixing facilities and other equipment shall be avoided.</li> <li>Mixing process and other associated material handling activities shall be properly scheduled to minimise potential cumulative noise impact on the nearby noise sensitive receivers.</li> <li>Construction Noise Permit shall be applied for the operation of powered mechanical equipment during restricted hours (if any).</li> </ul>							

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
	<p><u>Water Quality Mitigation Measures</u></p> <ul style="list-style-type: none"> <li>Stockpile of untreated soil shall be covered as far as practicable to prevent the contaminated material from leaching out. The leachate shall be discharged following the requirements of WPCO.</li> </ul> <p><u>Waste Mitigation Measures</u></p> <ul style="list-style-type: none"> <li>Treated oversize materials will be used as filling material for backfilling within the site. Sorted materials of size smaller than 5 cm will be collected and transferred to the mixing plant for further decontamination treatment.</li> <li>Stabilized soils shall be broken into suitable size for backfilling or reuse on site.</li> <li>A high standard of housekeeping shall be maintained within the mixing plant area.</li> <li>If necessary, there shall be clear and separated areas for stockpiling of untreated and treated materials.</li> </ul>							

\* Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Appendix 3.1

**Table A13.6 Implementation Schedule for Marine Ecology**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>Construction Phase</b>								
<i>For the Whole Project - Schedule 3 DP</i>								
S.9.7.2	Alternative design of the Trunk Road constructed in tunnel shall be adopted to avoid permanent reclamation in CBTS and ex-PWCA Basin.	-	CEDD/HyD	√				EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
<i>For DP3 - Reclamation Works</i>								
S.9.7.3	Translocation of those potentially affected coral colonies to the nearby suitable habitats such as Junk Bay is recommended. A detailed translocation plan (including translocation methodology, monitoring of transplanted corals, etc.) should be drafted and approval by AFCD during the detailed design stage of the Project.	Ex-PCWA Basin and along seawall next to a public pier which is about 250 m away from the CBTS	CEDD/HyD	√				EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S.9.7.4	<p>During dredging and filling operations, a number of mitigation measures to control water quality shall be adopted to confine sediment plume within reclamation area and protect marine fauna in proximity to the reclamation. The mitigation measures include the following:</p> <ul style="list-style-type: none"> <li>• Installation of silt curtains during dredging activities</li> <li>• Use of tightly-closed grab dredger</li> <li>• Reduction of dredging rate</li> <li>• Control of grab descending speed</li> <li>• Construction of leading edges of seawall in the early stages of the reclamation works</li> </ul>	Work site / during construction phase	Contractor		√			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
	<ul style="list-style-type: none"> <li>• Adoption of multiple-phase construction schedule</li> </ul>							

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
S.9.7.6	<p>To minimize potential disturbance impacts on the foraging ardeid population in the CBTS, particularly in the area near the A King Shipyard, appropriate mitigation measures shall be adopted particularly during the construction phase. The following measures are recommended:</p> <ul style="list-style-type: none"> <li>• Use of Quiet Mechanical Plant during the construction phase shall be adopted wherever possible.</li> <li>• Adoption of multiple-phase construction schedule.</li> <li>• General measures to reduce noise generated during the construction phase (see noise impact assessment) shall be effectively implemented.</li> </ul>	Work site / during construction phase	Contractor		√			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
S.9.7.7	Seawalls shall be constructed in advance around the reclamation areas within the area of the CBTS to screen adjacent feeding ground from construction phase activities, reduce noise disturbance to the associated seabirds and also to restrict access to this habitat adjacent to works areas by ship traffic.	Work site / during construction phase	Contractor		√			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.
S.9.7.8	Loss of artificial seawall habitats shall be reinstated by the construction of about 1 km vertical wave absorbing seawall along the coastlines of the new reclamation around the HKCEC and at North Point. The new seawalls are expected to provide large area of hard substrata for settlement and recruitment of intertidal fauna similar to those previously recorded from existing intertidal habitats.	Work site / during construction phase	Contractor		√			EIAO TM Annex 16 (Section 8.4) & EIAO Guidance Note No. 3/2002.

\*Des - Design, C - Construction, O - Operation, and Dec - Decommissioning

Appendix 3.1

**Table A13.7 Implementation Schedule for Landscape and Visual**

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
<b>Construction Phase</b>								
<b>For the Whole Project</b>								
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
<b>For DP1 – CWB (Within the Project Boundary)</b>								
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
<b>For DP2 – WDII Major Roads (Road P2)</b>								
Table 10.5	CM1 Topsoil, where identified, shall be stripped and stored for re-use in the construction of the soft landscape works, where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM2 Existing trees to be retained on site shall be carefully protected during construction.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM3 Trees unavoidably affected by the works shall be transplanted where practical.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM4 Compensatory tree planting shall be provided to compensate for felled trees.	Work site / During Construction Phase	Contractor	√	√			EIAO TM
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
<b>For DP3 – Reclamation Works</b>								
Table 10.5	CM5 Control of night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Table 10.5	CM6 Erection of decorative screen hoarding compatible with the surrounding setting.	Work site / During Construction Phase	Contractor		√			EIAO TM
<b>For DP5 – Wan Chai East Sewage Outfall</b>								
Refer to EIA-058/2001 Table 10.13	CM2 Minimisation of works areas.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM3 Erection of decorative hoardings.	Work site / During Construction Phase	Contractor		√			EIAO TM

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Refer to EIA-058/2001 Table 10.13	CM4 Control night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM5 Minimisation of disruption to public by effective programming of the works.	Work site / During Construction Phase	Contractor		√			EIAO TM
<b>For DP6 – Cross-Harbour Water Mains from Wan Chai to Tsim Sha Tsui</b>								
Refer to EIA-058/2001 Table 10.13	CM2 Minimisation of works areas.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM3 Erection of decorative hoardings.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM4 Control night-time lighting.	Work site / During Construction Phase	Contractor		√			EIAO TM
Refer to EIA-058/2001 Table 10.13	CM5 Minimisation of disruption to public by effective programming of the works.	Work site / During Construction Phase	Contractor		√			EIAO TM
<b>Operation Phase</b>								
<b>For the Whole Project - Schedule 3 DP</b>								
Table 10.6, Figure 10.5.1-10.5.5	OM1 Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	CEDD/HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM2 Shrub and Climbing Plants to soften proposed structures.	Work site / During Design Stage and Operation Phases	CEDD/HyD	√	√	√		ETWB TCW 2/2004

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 10.6, Figure 10.5.1-10.5.5	OM3 Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	CEDD/HyD/	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM4 Aesthetic design of proposed waterfront promenade.	Work site / During Design Stage and Operation Phases	CEDD <sup>4</sup>	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM5 Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	CEDD/HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM6 Aesthetic design of roadside amenity areas.	Work site / During Design Stage and Operation Phases	CEDD/HyD	√	√	√		ETWB TCW 2/2004
<b>For DP1 – CWB (Within the Project Boundary)</b>								
Table 10.6, Figure 10.5.1-10.5.5	OM1 Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM2 Shrub and Climbing Plants to soften proposed structures	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM3 Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM5 Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM6 Aesthetic design of roadside amenity areas.	Work site / During Design Stage and Operation Phases	HyD	√	√	√		ETWB TCW 2/2004
<b>For DP2 – WDII Major Roads (Road P2)</b>								

<sup>4</sup> CEDD will identify an implementation agent

Appendix 3.1

EIA Ref	Environmental Protection Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages*				Relevant Legislation and Guidelines
				Des	C	O	Dec	
Table 10.6, Figure 10.5.1-10.5.5	OM1 Aesthetic design of buildings and road-related structures, including viaducts, vent buildings, subways, footbridges and noise barriers and enclosure.	Work site / During Design Stage and Operation Phases	CEDD/HyD		√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM3 Buffer Tree and Shrub Planting to screen proposed roads and associated structures.	Work site / During Design Stage and Operation Phases	CEDD/HyD		√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM5 Aesthetic streetscape design.	Work site / During Design Stage and Operation Phases	CEDD/HyD		√	√		ETWB TCW 2/2004
Table 10.6, Figure 10.5.1-10.5.5	OM6 Aesthetic design of roadside amenity areas	Work site / During Design Stage and Operation Phases	CEDD/HyD		√	√		ETWB TCW 2/2004
<b>For DP3 – Reclamation Works</b>								
Table 10.6, Figure 10.5.1-10.5.5	OM4 Aesthetic design of proposed waterfront promenade.	Work site / During Design Stage and Operation Phases	CEDD <sup>5</sup>	√	√	√		ETWB TCW 2/2004

\*Des - Design, C - Construction, O – Operation, and Dec - Decommissioning

<sup>5</sup> CEDD will identify an implementation agent



***Appendix 4.1***

***Action and Limit Level***

**Action and Limit Level***Action and Limit Level for Noise Monitoring*

Time Period	Action Level	Limit Level
07:00 – 19:00 hours on normal weekdays	When one documented complaint is received.	75 dB(A) <sup>Note 1</sup>

Note 1:

- 70dB(A) and 65 dB(A) for schools during normal teaching periods and school examination periods, respectively.
- If works are to be carried out during the restricted hours, the conditions stipulated in the Construction Noise Permit (CNP) issued by the Noise Control Authority have to be followed.

*Action and Limit Level for Air Monitoring*

Monitoring Location	1-hour TSP Level in $\mu\text{g}/\text{m}^3$		24-hour TSP Level in $\mu\text{g}/\text{m}^3$	
	Action Level	Limit Level	Action Level	Limit Level
CMA1b <sup>Note 2</sup>	320.1	500	176.7	260
CMA2a	323.4	500	169.5	260
CMA3a <sup>Note 2</sup>	311.3	500	171.0	260
CMA4a	312.5	500	171.2	260
CMA5b <sup>Note 2</sup>	332.0	500	181.0	260
CMA6a <sup>Note 2</sup>	300.1	500	187.3	260

Note 2:

- As per facing owner's rejection in allowing the implementation of long-term air quality impact monitoring at their premises, alternative monitoring stations and justification were proposed for IEC verification and EPD approval.
- The established Action and Limit Levels from the baseline air monitoring will be adopted to the alternative monitoring stations.

*Action and Limit Level for Water Monitoring*

Parameters	Dry Season		Wet Season	
	Action	Limit	Action	Limit
<b>WSD Salt Water Intake</b>				
SS in $\text{mg L}^{-1}$	13.00	14.43	16.26	19.74
Turbidity in NTU	8.04	9.49	10.01	11.54
DO in mg/L	3.66	3.28	3.17	2.63
<b>Cooling Water Intake</b>				
SS in $\text{mg L}^{-1}$	15.00	22.13	18.42	27.54
Turbidity in NTU	9.10	10.25	11.35	12.71
DO in mg/L	3.36	2.73	3.02	2.44

Remarks:

- Action and Limit Level for the wet season are applied after the EPD approval of Updated EM&A Manual on 29 April 2011.

*Action and Limit Levels for Odour Patrol*

Parameters	Action	Limit
Odour Nuisance (from odour intensity analysis or odour patrol)	<ul style="list-style-type: none"> <li>• When two documented complaint are received; or</li> <li>• Odour Intensity of 2 is measured from odour intensity analysis.</li> </ul>	<ul style="list-style-type: none"> <li>• Five or more consecutive genuine documented complaints within a week; or</li> <li>• Odour Intensity of 3 or above is measured from odour intensity analysis.</li> </ul>



***Appendix 4.2***

***Copies of Calibration Certificates***

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION****Information supplied by customer:**

**CONTACT:** SAM LAM **WORK ORDER:** HK1510147  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 2015-05-22  
**DATE OF ISSUE:** 2015-06-01  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	22-May-15

## Remarks:

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1510147  
**DATE OF ISSUE:** 2015-06-01  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	22-May-15
<b>Date of next Calibration:</b>	22-Aug-15

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	3.86	-3.5
10	10.1	1.0
40	40.0	0.0
100	101	1.0
400	399	-0.3
1000	1000	0.0
	Tolerance Limit ( $\pm\%$ )	10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION****Information supplied by customer:**

**CONTACT:** SAM LAM **WORK ORDER:** HK1510319  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 21/8/2015  
**DATE OF ISSUE:** 26/8/2015  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** --

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	21-Aug-15

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1510319  
**DATE OF ISSUE:** 26/8/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203010
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	21-Aug-15
<b>Date of next Calibration:</b>	21-Nov-15

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	4.16	4.0
10	9.63	-3.7
40	41.5	3.8
100	96	-4.0
400	406	1.5
1000	998	-0.2
	<b>Tolerance Limit (±%)</b>	<b>10.0</b>

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

This report may not be reproduced except with prior written approval from Pilot Testing Limited.



**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**Information supplied by customer:**

**CONTACT:** SAM LAM **WORK ORDER:** HK1510256  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 08/07/2015  
**DATE OF ISSUE:** 15/07/2015  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** --

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203015
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	08/07/2015

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1510256  
**DATE OF ISSUE:** 15/07/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1203015
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	08/07/2015
<b>Date of next Calibration:</b>	08/10/2015

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	3.92	-2.0
10	10.3	3.0
40	38.5	-3.8
100	95.4	-4.6
400	387	-3.3
1000	996	-0.4
	<b>Tolerance Limit (±%)</b>	<b>10.0</b>

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION****Information supplied by customer:**

**CONTACT:** SAM LAM **WORK ORDER:** HK1510257  
**CLIENT:** LAM GEOTECHNICS LIMITED  
**DATE RECEIVED:** 08/07/2015  
**DATE OF ISSUE:** 15/07/2015  
**ADDRESS:** 11/F, CENTRE POINT, 181-185, GLOUCESTER ROAD,  
WANCHAI, HONG KONG  
**PROJECT:** ---

**METHOD OF PERFORMANCE CHECK/ CALIBRATION:**

Ref: APHA22nd ed 2130B

**COMMENTS**

It is certified that the item under performance check/calibration has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.

<b>Scope of Test:</b>	Turbidity
<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1309192
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	08/07/2015

**Remarks:**

This is the Final Report. Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

Mr. Peter Lee  
Director

This report may not be reproduced except with prior written approval from Pilot Testing Limited.

**REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION**

**WORK ORDER:** HK1510257  
**DATE OF ISSUE:** 15/07/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type:</b>	Turbidimeter
<b>Brand Name:</b>	Xin Rui
<b>Model No.:</b>	WGZ-3B
<b>Serial No.:</b>	1309192
<b>Equipment No.:</b>	---
<b>Date of Calibration:</b>	08/07/2015
<b>Date of next Calibration:</b>	08/10/2015

**Parameters:****Turbidity**Method Ref: APHA 22<sup>nd</sup> ed. 2130B

Expected Reading (NTU)	Display Reading (NTU)	Tolerance (%)
0	0.00	---
4	4.11	2.8
10	9.79	-2.1
40	42.4	6.0
100	103	3.0
400	387	-3.3
1000	982	-1.8
	<b>Tolerance Limit (±%)</b>	<b>10.0</b>

Remark: "Displayed Reading" presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.

---

This report may not be reproduced except with prior written approval from Pilot Testing Limited.



## EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

**Report No.** : HK1510258  
**Project Name** : EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT  
**Date of Issue** : 20/07/2015  
  
**Customer** : LAM GEOTECHNICS LIMITED  
**Address** : 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG  


---

**Calibration Job No.** : HK1510258  
**Test Item No.** : HK1510258-01  
**Test Item Details**  
**Test Item Description** : Multifunctional Meter  
**Manufacturer** : YSI  
**Model No.** : Professional Plus  
**Serial No.** : 14E100105  
**Performance Method** : Checked according to in-house method CAL005  
(References: Temperature (Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value (APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B ) , Dissolved oxygen (APHA 19e 4500-O,C))  
**Test Item Receipt Date** : 14-Jul-15  
**Test Item Calibration Date** : 15-Jul-15  
**Test Period** : 14/07/2015 - 20/07/2015  


---

- Notes :
1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
  2. Results relate to item(s) as received.
  3.  $\pm$  indicates the tolerance limit
  4. N/A = Not applicable
  5. APHA - American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF. USA
  6. DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
  7. Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory :

Mr. Peter Lee  
(Director)

Issue Date:

20/07/2015

Pilot Testing Limited

Address: Room B12, Block B, 5/F, Tonic Industrial Centre, 19 Lam Hing Street, Kowloon Bay, Kowloon  
Tel: (852) 2527 6691 email: test@pilot-testing.com


**REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

**WORK ORDER:** HK1510258  
**DATE OF ISSUE:** 20/07/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type</b>	Multifunctional Meter
<b>Manufacturer</b>	YSI
<b>Model No.</b>	Professional Plus
<b>Serial No.</b>	14E100105
<b>Date of Calibration</b>	15-Jul-15
<b>Date of next Calibration</b>	15-Oct-15

**Parameters:**

**Temperature (Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)**

Reference Reading (°C)	Display Reading (°C)	Deviation (°C)
9.6	10.5	+0.9
19.9	20.3	+0.4
32.0	31.5	-0.5
Tolerance Limit		±2.0

**pH Value (Method Ref: APHA21e, 4500H:B)**

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	3.92	4.07	+0.15
7.0	6.94	6.97	+0.03
10.0	9.91	10.03	+0.12
Tolerance Limit			±0.20

**Conductivity (Method Ref: APHA 19e, 2510)**

KCl concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	--
0.1000	12.89	12.70	-1.45
0.2000	24.80	24.53	-1.08
0.5000	58.67	58.09	-0.99
Tolerance Limit			±2.0

**Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)**

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
8.41	8.46	+0.05
3.18	3.36	+0.18
1.06	1.09	+0.03
Tolerance Limit		±0.20

- Remarks:
- (1) Maximum tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.
  - (2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.
  - (3) Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

- End of Report -



## EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

**Report No.** : HK1510261  
**Project Name** : EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT  
**Date of Issue** : 24/07/2015  
  
**Customer** : LAM GEOTECHNICS LIMITED  
**Address** : 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG

---

**Calibration Job No.** : HK1510261  
**Test Item No.** : HK1510261-01  
**Test Item Details**  
**Test Item Description** : Multifunctional Meter  
**Manufacturer** : YSI  
**Model No.** : Professional Plus  
**Serial No.** : 14M100277  
**Performance Method** : Checked according to in-house method CAL005  
 (References: Temperature (Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value (APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B ) , Dissolved oxygen (APHA 19e 4500-O,C))  
  
**Test Item Receipt Date** : 17-Jul-15  
**Test Item Calibration Date** : 17-Jul-15  
**Test Period** : 17/07/2015 - 24/07/2015

---

- Notes :
1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
  2. Results relate to item(s) as received.
  3.  $\pm$  indicates the tolerance limit
  4. N/A = Not applicable
  5. APHA - American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF. USA
  6. DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
  7. Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory :

Mr. Peter Lee  
(Director)

Issue Date:

24/07/2015


**REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

**WORK ORDER:** HK1510261  
**DATE OF ISSUE:** 24/07/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type</b>	Multifunctional Meter
<b>Manufacturer</b>	YSI
<b>Model No.</b>	Professional Plus
<b>Serial No.</b>	14M100277
<b>Date of Calibration</b>	17-Jul-15
<b>Date of next Calibration</b>	17-Oct-15

**Parameters:**

**Temperature (Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)**

Reference Reading (°C)	Display Reading (°C)	Deviation (°C)
10.3	10.4	+0.1
19.9	20.0	+0.1
29.5	29.4	-0.1
Tolerance Limit		±2.0

**pH Value (Method Ref: APHA21e, 4500H:B)**

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	4.02	4.04	+0.02
7.0	6.98	7.07	+0.09
10.0	9.94	10.06	+0.12
Tolerance Limit			±0.20

**Conductivity (Method Ref: APHA 19e, 2510)**

KCl concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	--
0.1000	12.89	12.66	-1.79
0.2000	24.80	25.12	+1.29
0.5000	58.67	58.77	+0.17
Tolerance Limit			±2.0

**Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)**

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
6.34	6.42	+0.08
3.10	3.17	+0.07
1.51	1.43	-0.08
Tolerance Limit		±0.20

- Remarks:
- (1) Maximum tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.
  - (2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.
  - (3) Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

- End of Report -



## EQUIPMENT PERFORMANCE CHECK / CALIBRATION REPORT

**Report No.** : HK1510259  
**Project Name** : EQUIPMENT PERFORMANCE CHECK/CALIBRATION REPORT  
**Date of Issue** : 20/07/2015  
  
**Customer** : LAM GEOTECHNICS LIMITED  
**Address** : 11/F., CENTRE POINT, 181-185 GLOUCESTER ROAD, WAN CHAI, HONG KONG

---

**Calibration Job No.** : HK1510259  
**Test Item No.** : HK1510259-01  
**Test Item Details**  
**Test Item Description** : Multifunctional Meter  
**Manufacturer** : YSI  
**Model No.** : Professional Plus  
**Serial No.** : 11F100420  
**Performance Method** : Checked according to in-house method CAL005  
 (References: Temperature (Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure), pH value (APHA 21e 4500H:B), Salinity (Refer to Conductivity APHA 19e 2510B ) , Dissolved oxygen (APHA 19e 4500-O,C))  
  
**Test Item Receipt Date** : 14-Jul-15  
**Test Item Calibration Date** : 15-Jul-15  
**Test Period** : 14/7/2015 - 20/7/2015

---

- Notes :
1. This report shall not be reproduced, except in full, without prior approval from Pilot Testing Limited.
  2. Results relate to item(s) as received.
  3. ± indicates the tolerance limit
  4. N/A = Not applicable
  5. APHA - American Public Health Association, American Water Works Association and Water Environment Federation, Standard Methods for the Examination of Water and Wastewater, APHA-AWWA-WEF. USA
  6. DO, pH, salinity and temperature performance check was conducted by Pilot Testing Limited.
  7. Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

Approved Signatory :

Mr. Peter Lee  
(Director)

Issue Date:

20/07/2015


**REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION**

**WORK ORDER:** HK1510259  
**DATE OF ISSUE:** 20/07/2015  
**CLIENT:** LAM GEOTECHNICS LIMITED

<b>Equipment Type</b>	Multifunctional Meter
<b>Manufacturer</b>	YSI
<b>Model No.</b>	Professional Plus
<b>Serial No.</b>	11F100420
<b>Date of Calibration</b>	15-Jul-15
<b>Date of next Calibration</b>	15-Oct-15

**Parameters:**

**Temperature (Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No.3 Second edition March 2008: Working Thermometer Calibration Procedure)**

Reference Reading (°C)	Display Reading (°C)	Deviation (°C)
9.8	10.1	+0.3
20.2	20.3	+0.1
30.1	29.5	-0.6
Tolerance Limit		±2.0

**pH Value (Method Ref: APHA21e, 4500H:B)**

Expected Reading (pH unit)	Reference Reading (pH unit)	Display Reading (pH unit)	Deviation (pH unit)
4.0	4.02	4.08	+0.06
7.0	6.92	6.87	-0.05
10.0	10.10	9.98	-0.12
Tolerance Limit			±0.20

**Conductivity (Method Ref: APHA 19e, 2510)**

KCl concentration (mol/L)	Reference Reading (ms/cm)	Display Reading (ms/cm)	Deviation (%)
0.0000	0.00	0.00	--
0.1000	12.89	12.92	+0.23
0.2000	24.80	24.52	-1.13
0.5000	58.67	59.10	+0.73
Tolerance Limit			±2.0

**Dissolved Oxygen (DO) (Method Ref: APHA 19e, 4500-O, C)**

Reference DO reading (mg/L)	DO reading od DO probe (mg/L)	Deviation (mg/L)
8.83	8.90	+0.07
5.23	5.26	+0.03
1.17	1.24	+0.07
Tolerance Limit		±0.20

- Remarks:
- (1) Maximum tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of Pilot Testing Limited will be followed.
  - (2) Displayed reading presents the figures shown on item under calibration/checking regardless of equipment precision or significant figures.
  - (3) Because of high sensitivity and ease of measurement, the conductivity method (according to APHA 19e 2510) is used to determine salinity.

- End of Report -



TISCH ENVIRONMENTAL, INC.  
 145 SOUTH MIAMI AVE  
 VILLAGE OF CLEVELAND, OH  
 45002  
 513.467.9000  
 877.263.7610 TOLL FREE  
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Jun 30, 2015 Rootsmeter S/N 0438320 Ta (K) - 296  
 Operator Tisch Orifice I.D. - 0005 Pa (mm) - 749.3

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER	ORFICE
					DIFF Hg (mm)	DIFF H2O (in.)
1	NA	NA	1.00	1.3930	3.2	2.00
2	NA	NA	1.00	0.9800	6.4	4.00
3	NA	NA	1.00	0.8790	7.9	5.00
4	NA	NA	1.00	0.8350	8.7	5.50
5	NA	NA	1.00	0.6900	12.7	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
0.9883	0.7095	1.4090	0.9957	0.7148	0.8889
0.9841	1.0042	1.9926	0.9915	1.0117	1.2570
0.9820	1.1172	2.2278	0.9894	1.1256	1.4054
0.9810	1.1749	2.3365	0.9884	1.1837	1.4740
0.9757	1.4141	2.8179	0.9830	1.4247	1.7777
Qstd slope (m) = 2.00072			Qa slope (m) = 1.25282		
intercept (b) = -0.01209			intercept (b) = -0.00763		
coefficient (r) = 0.99995			coefficient (r) = 0.99995		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)  
 Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]  
 Qa = Va/Time

For subsequent flow rate calculations:

Qstd = 1/m { [SQRT(H2O(Pa/760) (298/Ta))] - b }  
 Qa = 1/m { [SQRT H2O(Ta/Pa)] - b }



Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA1b  
 Equipment no. : EL452  
 Calibration Date : 10-Jun-15  
 Calibration Due Date : 10-Aug-15

#### CALIBRATION OF CONTINUOUS FLOW RECORDER

Ambient Condition			
Temperature, T <sub>a</sub>	303	Kelvin	Pressure, P <sub>a</sub>
			1007 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$\left( \frac{H \times P_a}{1013.3 \times 298 / T_a} \right)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	6.1	6.1	12.2	1.7339	60	59.3176
2	4.7	4.7	9.4	1.5220	54	53.3859
3	3.8	3.8	7.6	1.3686	48	47.4541
4	2.3	2.3	4.6	1.0648	38	37.5678
5	1.4	1.4	2.8	0.8308	30	29.6588

By Linear Regression of Y on X

Slope, m = 33.1850      Intercept, b = 2.2031  
 Correlation Coefficient\* = 0.9994  
 Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar      Checked by : Derek Lo  
 Date : 10-Jun-15      Date : 10-Jun-15



Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA1b  
 Equipment no. : EL452  
 Calibration Date : 10-Aug-15  
 Calibration Due Date : 10-Oct-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	301	Kelvin	Pressure, P <sub>a</sub>
			1005 mmHg

Orifice Transfer Standard Information			
Equipment No.	EL086	Slope, m <sub>c</sub>	2.00072
		Intercept, b <sub>c</sub>	-0.01209
Last Calibration Date	30-Jun-15	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$	
Next Calibration Date	30-Jun-16		

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	5.9	5.9	11.8	1.7074	60	59.4552
2	4.8	4.8	9.6	1.5406	52	51.5279
3	3.8	3.8	7.6	1.3714	45	44.5914
4	2.5	2.5	5.0	1.1135	36	35.6731
5	1.6	1.6	3.2	0.8920	28	27.7458

By Linear Regression of Y on X

Slope, m = 38.3067      Intercept, b = -6.9577

Correlation Coefficient\* = 0.9980

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar      Checked by : Derek Lo  
 Date : 10-Aug-15      Date : 10-Aug-15





Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA2a Calibration Date : 10-Aug-15  
 Equipment no. : EL449 Calibration Due Date : 10-Oct-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	301	Kelvin	Pressure, P <sub>a</sub>
			1005 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	2.00072	Intercept, b <sub>c</sub>	-0.01209
Last Calibration Date	30-Jun-15	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	30-Jun-16				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	5.8	5.8	11.6	1.6929	59	58.4643
2	4.6	4.6	9.2	1.5083	50	49.5460
3	3.7	3.7	7.4	1.3534	43	42.6096
4	2.5	2.5	5.0	1.1135	34	33.6913
5	1.5	1.5	3.0	0.8639	22	21.8003

By Linear Regression of Y on X

Slope, m = 43.3899 Intercept, b = -15.4622

Correlation Coefficient\* = 0.9990

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar Checked by : Derek Lo  
 Date : 10-Aug-15 Date : 10-Aug-15



Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA3a  
 Equipment no. : EL333  
 Calibration Date : 10-Jun-15  
 Calibration Due Date : 10-Aug-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	303	Kelvin	Pressure, P <sub>a</sub>
			1007 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	5.6	5.6	11.2	1.6613	52	51.4086
2	4.5	4.5	9.0	1.4893	48	47.4541
3	3.4	3.4	6.8	1.2946	40	39.5451
4	2.2	2.2	4.4	1.0414	34	33.6133
5	1.4	1.4	2.8	0.8308	28	27.6816

By Linear Regression of Y on X

Slope, m = 28.9984      Intercept, b = 3.3019

Correlation Coefficient\* = 0.9964

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar      Checked by : Derek Lo  
 Date : 10-Jun-15      Date : 10-Jun-15





Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA4a Calibration Date : 10-Jun-15  
 Equipment no. : EL390 Calibration Due Date : 10-Aug-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	303	Kelvin	Pressure, P <sub>a</sub>
			1007 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	5.9	5.9	11.8	1.7053	57	56.3517
2	4.7	4.7	9.4	1.5220	52	51.4086
3	3.6	3.6	7.2	1.3321	44	43.4996
4	2.3	2.3	4.6	1.0648	34	33.6133
5	1.4	1.4	2.8	0.8308	26	25.7043

By Linear Regression of Y on X

Slope, m = 35.8979 Intercept, b = -4.2281

Correlation Coefficient\* = 0.9988

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar Checked by : Derek Lo  
 Date : 10-Jun-15 Date : 10-Jun-15



Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA4a Calibration Date : 10-Aug-15  
 Equipment no. : EL390 Calibration Due Date : 10-Oct-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	301	Kelvin	Pressure, P <sub>a</sub>
			1005 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	2.00072	Intercept, b <sub>c</sub>	-0.01209
Last Calibration Date	30-Jun-15	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	30-Jun-16				

Calibration of TSP						
Calibration Point	Manometer Reading H (inches of water)			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	5.7	5.7	11.4	1.6783	58	57.4734
2	4.6	4.6	9.2	1.5083	51	50.5370
3	3.6	3.6	7.2	1.3350	45	44.5914
4	2.4	2.4	4.8	1.0912	34	33.6913
5	1.5	1.5	3.0	0.8639	25	24.7730

By Linear Regression of Y on X

Slope, m = 40.2813 Intercept, b = -9.9646

Correlation Coefficient\* = 0.9994

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar Checked by : Derek Lo  
 Date : 10-Aug-15 Date : 10-Aug-15



Lam Geotechnics Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : CMA5b  
 Equipment no. : EL222

Calibration Date : 02-Jun-15  
 Calibration Due Date : 02-Aug-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	303	Kelvin	Pressure, P <sub>a</sub>
			1009 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041
Last Calibration Date	14-Jul-14	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	14-Jul-15				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	6.3	6.3	12.6	1.7639	65	64.3245
2	4.8	4.8	9.6	1.5397	58	57.3973
3	3.6	3.6	7.2	1.3334	52	51.4596
4	2.3	2.3	4.6	1.0658	42	41.5636
5	1.4	1.4	2.8	0.8316	30	29.6883

By Linear Regression of Y on X

Slope, m = 36.5046      Intercept, b = 1.1799  
 Correlation Coefficient\* = 0.9934  
 Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar  
 Date : 02-Jun-15

Checked by : Derek Lo  
 Date : 02-Jun-15



Lam Geotechnics Limited

**Calibration Data for High Volume Sampler (TSP Sampler)**

Location : CMA5b Calibration Date : 01-Aug-15  
 Equipment no. : EL222 Calibration Due Date : 01-Oct-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	302	Kelvin	Pressure, P <sub>a</sub>
			1011 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	2.00072	Intercept, b <sub>c</sub>	-0.01209
Last Calibration Date	30-Jun-15	$(H \times P_a / 1013.3 \times 298 / T_a)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	30-Jun-16				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC (W(P <sub>a</sub> /1013.3x298/T <sub>a</sub> ) <sup>1/2</sup> /35.31) Y-axis
	(up)	(down)	(difference)			
1	5.5	5.5	11.0	1.6509	60	59.5336
2	4.3	4.3	8.6	1.4604	55	54.5725
3	3.4	3.4	6.8	1.2993	49	48.6191
4	2.3	2.3	4.6	1.0697	40	39.6891
5	1.5	1.5	3.0	0.8650	32	31.7513

By Linear Regression of Y on X

Slope, m = 35.9878 Intercept, b = 1.1624  
 Correlation Coefficient\* = 0.9974  
 Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient &lt; 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar Checked by : Derek Lo  
 Date : 01-Aug-15 Date : 01-Aug-15



Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA6a  
 Equipment no. : EL448  
 Calibration Date : 10-Jun-15  
 Calibration Due Date : 10-Aug-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition						
Temperature, T <sub>a</sub>	303	Kelvin	Pressure, P <sub>a</sub>	1007	mmHg	
Orifice Transfer Standard Information						
Equipment No.	EL086	Slope, m <sub>c</sub>	1.99175	Intercept, b <sub>c</sub>	-0.00041	
Last Calibration Date	14-Jul-14	$\left( \frac{H \times P_a}{1013.3 \times 298 / T_a} \right)^{1/2}$ $= m_c \times Q_{std} + b_c$				
Next Calibration Date	14-Jul-15					
Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC $(W(P_a/1013.3 \times 298/T_a)^{1/2}/35.31)$ Y-axis
	(up)	(down)	(difference)			
1	5.8	5.8	11.6	1.6908	55	54.3745
2	4.6	4.6	9.2	1.5057	50	49.4314
3	3.5	3.5	7.0	1.3135	44	43.4996
4	2.3	2.3	4.6	1.0648	35	34.6020
5	1.4	1.4	2.8	0.8308	28	27.6816
By Linear Regression of Y on X						
Slope, m		=	31.6381	Intercept, b		= 1.3862
Correlation Coefficient*		=	0.9990			
Calibration Accepted		=	Yes/No**			

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar  
 Date : 10-Jun-15  
 Checked by : Derek Lo  
 Date : 10-Jun-15



Lam Geotechnics Limited

### Calibration Data for High Volume Sampler (TSP Sampler)

Location : CMA6a  
 Equipment no. : EL448  
 Calibration Date : 10-Aug-15  
 Calibration Due Date : 10-Oct-15

**CALIBRATION OF CONTINUOUS FLOW RECORDER**

Ambient Condition			
Temperature, T <sub>a</sub>	301	Kelvin	Pressure, P <sub>a</sub>
			1005 mmHg

Orifice Transfer Standard Information					
Equipment No.	EL086	Slope, m <sub>c</sub>	2.00072	Intercept, b <sub>c</sub>	-0.01209
Last Calibration Date	30-Jun-15	$\left( H \times P_a / 1013.3 \times 298 / T_a \right)^{1/2}$ $= m_c \times Q_{std} + b_c$			
Next Calibration Date	30-Jun-16				

Calibration of TSP						
Calibration Point	Manometer Reading			Q <sub>std</sub> (m <sup>3</sup> / min.) X-axis	Continuous Flow Recorder, W (CFM)	IC $(W(P_a/1013.3 \times 298/T_a)^{1/2}/35.31)$ Y-axis
	(up)	(down)	(difference)			
1	6.2	6.2	12.4	1.7501	58	57.4734
2	4.9	4.9	9.8	1.5565	52	51.5279
3	3.8	3.8	7.6	1.3714	45	44.5914
4	2.5	2.5	5.0	1.1135	36	35.6731
5	1.5	1.5	3.0	0.8639	30	29.7276

By Linear Regression of Y on X

Slope, m = 32.1012      Intercept, b = 1.0688

Correlation Coefficient\* = 0.9974

Calibration Accepted = Yes/No\*\*

\* if Correlation Coefficient < 0.990, check and recalibration again.

\*\* Delete as appropriate.

Remarks : \_\_\_\_\_

Calibrated by : LuLu Mar      Checked by : Derek Lo  
 Date : 10-Aug-15      Date : 10-Aug-15



***Appendix 5.1***

***Monitoring Schedules for Reporting Month and Coming Reporting Month***

Contract No. HK/2011/07  
Wan Chai Development Phase II and Central-Wan Chai Bypass  
Sampling, Field Measurement and Testing Works (Stage 2)  
Environmental Monitoring Schedule  
August 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		28-Jul	29-Jul	30-Jul	31-Jul	1-Aug
		24hr TSP	24hr TSP (CMA1b) 1hr TSP			
		Impact WQM Mid-ebb 10:04 Mid-flood 17:21		Impact WQM Mid-ebb 11:25 Mid-flood 18:35		Impact WQM Mid-ebb 12:55 Mid-flood 19:48
2-Aug	3-Aug	4-Aug	5-Aug	6-Aug	7-Aug	8-Aug
	24hr TSP Noise (daytime) (M3a, M4b, M6) Impact WQM Mid-ebb 14:23 Mid-flood 21:08	Odour Patrol 1hr TSP Noise (daytime) (M1a, M2b, M5b)				
			Impact WQM Mid-flood 9:39 Mid-ebb 15:55		Impact WQM Mid-flood 12:06 Mid-ebb 17:52	
9-Aug	10-Aug	11-Aug	12-Aug	13-Aug	14-Aug	15-Aug
	Noise (daytime) (M2b, M3a, M4b) Impact WQM Mid-ebb 9:35 Mid-flood 16:40	Noise (daytime) (M1a, M5b, M6)			24hr TSP	1hr TSP
			Impact WQM Mid-ebb 11:07 Mid-flood 18:06		Impact WQM Mid-ebb 12:22 Mid-flood 19:08	
16-Aug	17-Aug	18-Aug	19-Aug	20-Aug	21-Aug	22-Aug
	Noise (daytime) (M1a, M2b) Impact WQM Mid-flood 7:29 Mid-ebb 14:00	Odour Patrol Noise (daytime) (M3a, M4b, M5b, M6)		24hr TSP	1hr TSP	
			Impact WQM Mid-flood 8:44 Mid-ebb 15:04		Impact WQM Mid-flood 10:15 Mid-ebb 16:18	
23-Aug	24-Aug	25-Aug	26-Aug	27-Aug	28-Aug	29-Aug
	Noise (daytime) (M1a, M2b, M3a, M4b, M5b, M6)		24hr TSP	24hr TSP (CMA1b) 1hr TSP	1hr TSP (CMA6a)	24hr TSP (CMA6a)
		Impact WQM Mid-ebb 8:49 Mid-flood 16:22		Impact WQM Mid-ebb 10:16 Mid-flood 17:33		

Remarks: With respect to the construction stage and access condition of Ex-PCWAW and the potential DO concern within the area, the suspended Enhance DO monitoring within Ex-PCWAW area at the Enhance DO monitoring station Ex-PCWA-SE was resumed on 10 August 2015 at the finely adjusted monitoring location.

Contract No. HK/2011/07  
Wan Chai Development Phase II and Central-Wan Chai Bypass  
Sampling, Field Measurement and Testing Works (Stage 2)  
Tentative Environmental Monitoring Schedule  
September 2015

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
					28-Aug	29-Aug
						Impact WQM Mid-ebb 11:50 Mid-flood 16:37
30-Aug	31-Aug	1-Sep	2-Sep	3-Sep	4-Sep	5-Sep
	Noise (daytime) Impact WQM Mid-ebb 13:20 Mid-flood 19:49	Odour Patrol  24hr TSP  Noise (daytime)	1hr TSP  Impact WQM Mid-flood 14:48 Mid-ebb 21:07		Impact WQM Mid-flood 10:38 Mid-ebb 16:29	
6-Sep	7-Sep	8-Sep	9-Sep	10-Sep	11-Sep	12-Sep
	24hr TSP  Noise (daytime)  Impact WQM Mid-ebb 8:08 Mid-flood 15:34	1hr TSP  Noise (daytime)	Impact WQM Mid-ebb 10:03 Mid-flood 17:07		Impact WQM Mid-ebb 11:24 Mid-flood 18:03	24hr TSP
13-Sep	14-Sep	15-Sep	16-Sep	17-Sep	18-Sep	19-Sep
	1hr TSP  Noise (daytime)  Impact WQM Mid-flood 13:04 Mid-ebb 19:12	Odour Patrol  Noise (daytime)	Impact WQM Mid-flood 14:07 Mid-ebb 20:05		24hr TSP  Impact WQM Mid-flood 15:15 Mid-ebb 21:01	1hr TSP
20-Sep	21-Sep	22-Sep	23-Sep	24-Sep	25-Sep	26-Sep
	Noise (daytime)	Noise (daytime)  Impact WQM Mid-ebb 6:34 Mid-flood 14:37		24hr TSP  Impact WQM Mid-ebb 8:54 Mid-flood 16:20	1hr TSP	Mid-ebb 10:39 Mid-flood 17:25



***Appendix 5.2***

***Noise Monitoring Results and Graphical Presentations***



**Noise Monitoring Result**

**Day Time (0700 - 1900hrs on normal weekdays)**

Location: M1a - Harbour Road Sports Centre

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
04/08/15	13:17	Fine	72.9	75.5	68.5	72	65	75
11/08/15	13:27	Fine	72.7	75.5	66.5	72	63	75
17/08/15	9:00	Fine	72.1	74.6	69.3	72	72	75
24/08/15	14:35	Fine	73.4	76.0	68.5	72	67	75

Location: M2b - Noon-day gun area

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
04/08/15	13:55	Fine	69.2	71.0	66.0	68	64	75
10/08/15	13:00	Cloudy	67.0	69.0	65.5	68	67	75
17/08/15	10:15	Fine	69.7	72.3	66.4	68	66	75
24/08/15	15:10	Fine	66.9	68.0	64.0	68	67	75

Location: M3a - Tung Lo Wan Fire Station

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
03/08/15	9:28	Fine	65.4	66.5	63.5	69	65	75
10/08/15	13:35	Cloudy	67.2	69.0	64.5	69	67	75
18/08/15	13:00	Fine	66.1	67.3	65.0	69	66	75
24/08/15	15:50	Fine	66.3	67.0	65.0	69	66	75

Location: M4b - Victoria Centre

Date	Time	Weather	Measurement Noise Level			Baseline Noise Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30min)								
03/08/15	10:01	Fine	65.6	67.0	63.5	67	66	75
10/08/15	14:15	Cloudy	65.2	66.0	63.0	67	65	75
18/08/15	13:39	Fine	66.5	67.8	64.8	67	67	75
24/08/15	16:40	Fine	66.2	67.5	64.0	67	66	75

Location: M5b - City Garden

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30min)								
04/08/15	14:37	Fine	65.4	66.5	63.0	68	65	75
11/08/15	8:00	Fine	67.8	69.0	66.0	68	68	75
18/08/15	10:24	Fine	71.3	72.5	68.5	68	69	75
24/08/15	9:42	Fine	73.0	73.1	69.5	68	71	75




Location: M6 - HK Baptist Church Henrietta Secondary School

Date	Time	Weather	Measurement Noise Level			Baseline Level	Construction Noise Level	Limit Level
			Leq	L10	L90	Leq	Leq	Leq
Unit: dB(A), (30-min)								
03/08/15	11:12	Fine	68.1	69.0	66.0	71	68	70
11/08/15	8:38	Fine	67.5	68.5	65.3	71	68	70
18/08/15	11:05	Fine	68.1	69.5	66.0	71	68	70
24/08/15	10:20	Fine	68.8	70.0	66.0	71	69	70



Graphic Presentation of Noise Monitoring Result




Day Time (0700 - 1900hrs on normal weekdays)

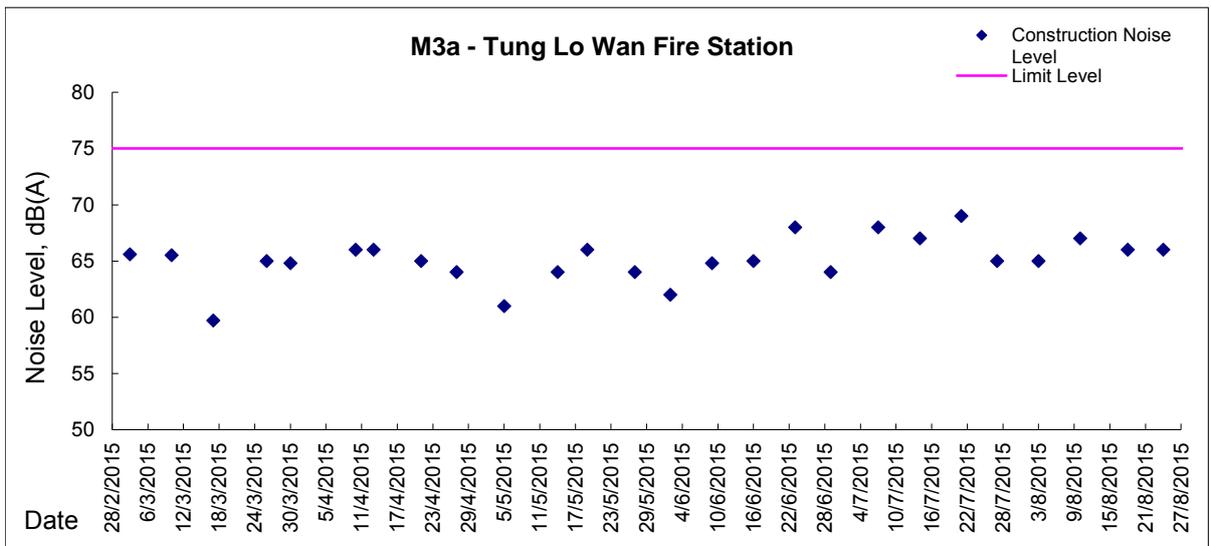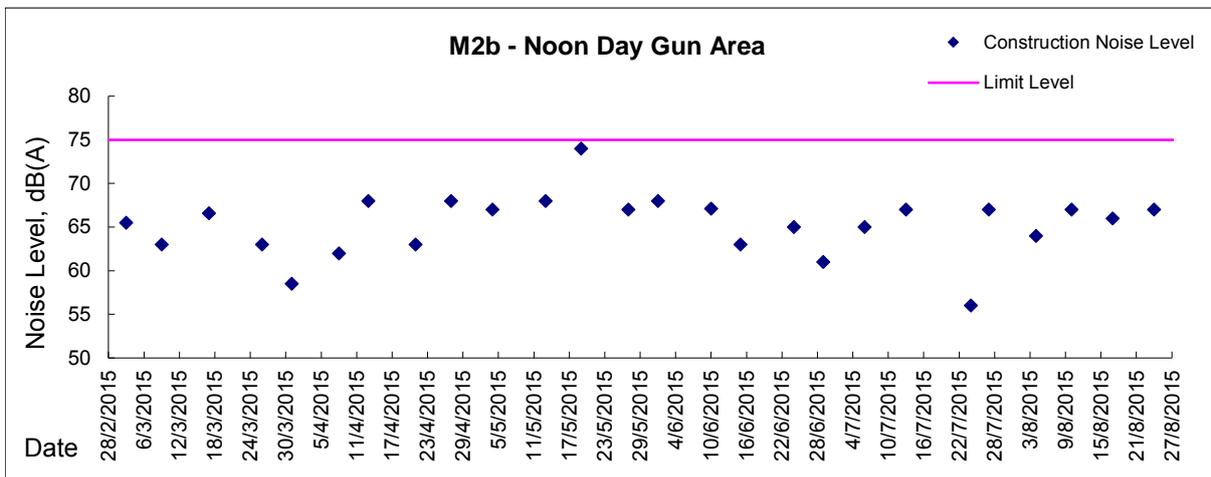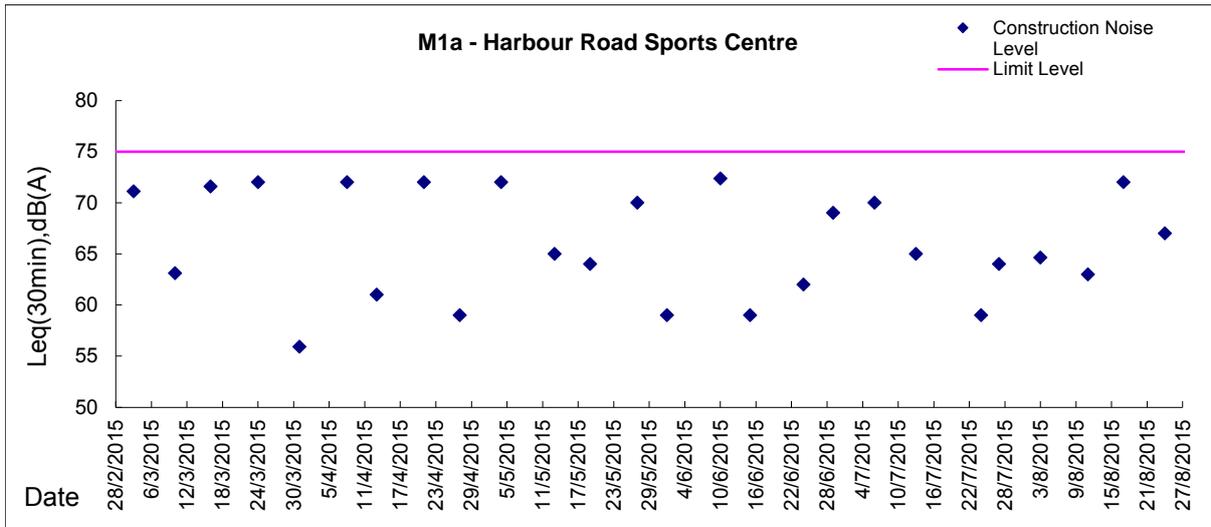



Graphic Presentation of Noise Monitoring Result

Day Time (0700 - 1900hrs on normal weekdays)

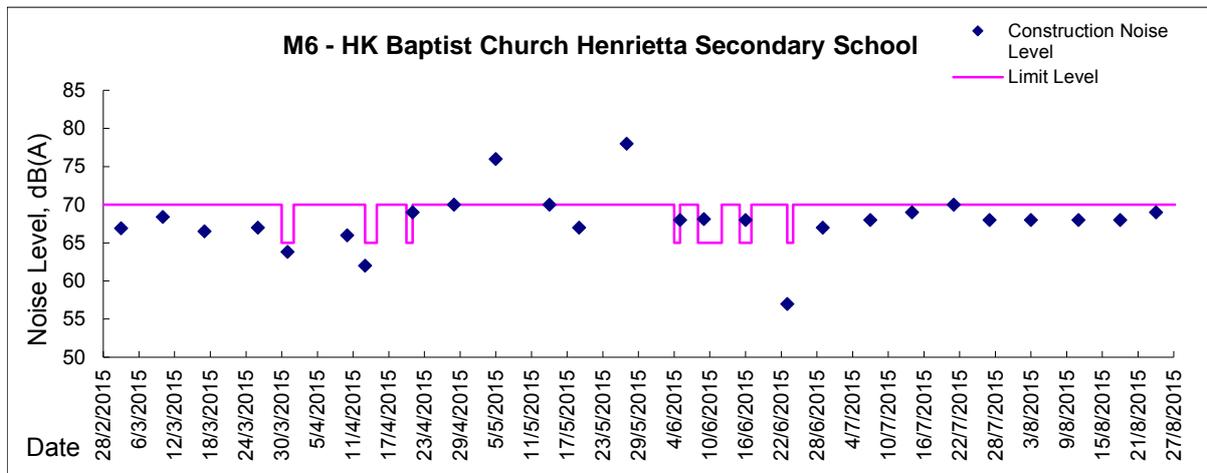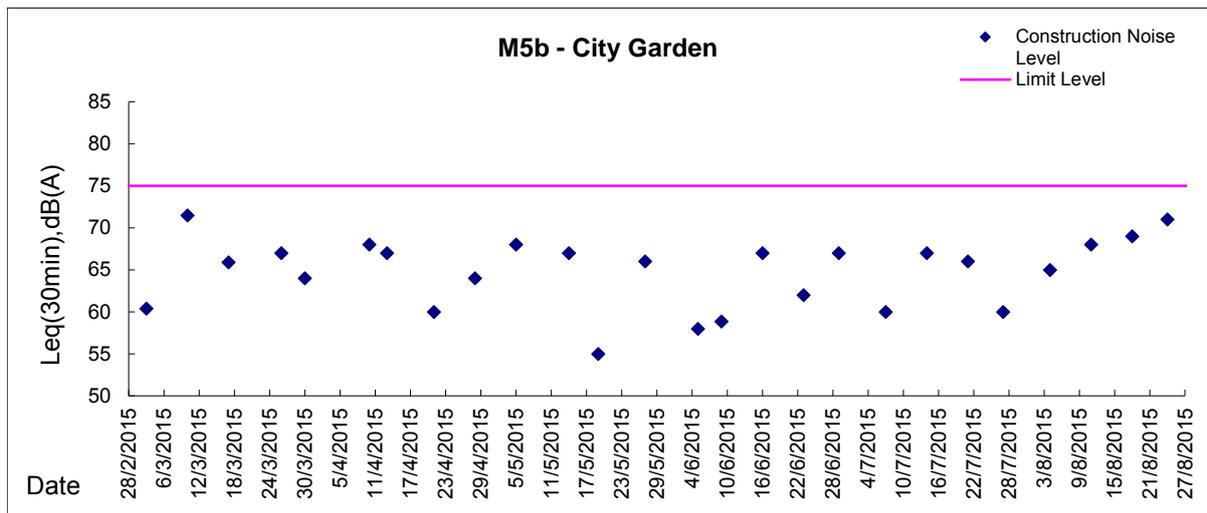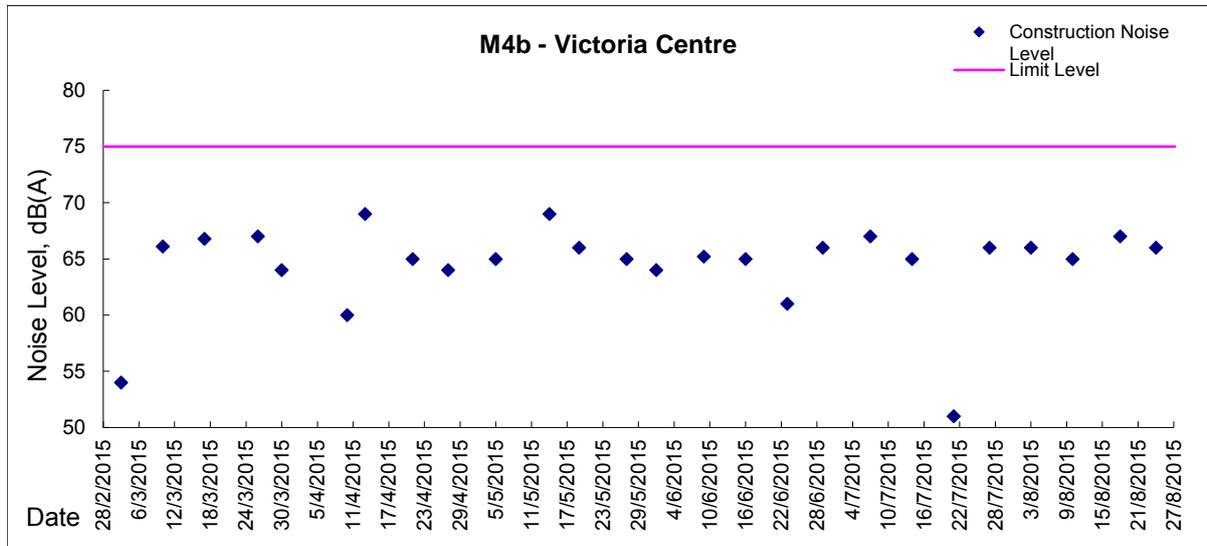



***Appendix 5.3***

***Air Quality Monitoring Results and Graphical Presentations, and odour Patrol Results***



Location: CMA1b - Oil Street Site Office

Report on 24-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 176.7

Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
29-Jul-15	11:30	Fine	012793	2.8218	2.9064	16738.23	16762.23	24.00	1.14	1.14	1.14	1645	51.4
3-Aug-15	8:00	Fine	012727	2.8461	2.9852	16762.23	16786.23	24.00	1.14	1.14	1.14	1640	84.8
8-Aug-15	8:00	Fine	012723	2.8412	3.0555	6789.23	6813.23	24.00	1.22	1.22	1.22	1752	122.3
14-Aug-15	8:00	Cloudy	012807	2.8183	2.9880	6816.23	6840.23	24.00	1.23	1.23	1.23	1769	95.9
20-Aug-15	8:00	Cloudy	012659	2.8125	3.0637	6843.33	6867.33	24.00	1.22	1.22	1.22	1761	142.7
27-Aug-15	13:00	Cloudy	012997	2.7963	2.9870	6873.82	6897.82	24.00	1.23	1.23	1.23	1766	108.0

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 28 July and 26 August 2015 to 29 July and 27 August 2015 respectively.

Report on 1-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 320.1

Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
29-Jul-15	8:02	Fine	012798	2.8297	2.8351	16735.22	16736.22	1.00	1.14	1.14	1.14	69	78.7
29-Jul-15	9:06	Fine	012796	2.8260	2.8311	16736.22	16737.22	1.00	1.14	1.14	1.14	69	74.4
29-Jul-15	10:13	Fine	012794	2.8363	2.8405	16737.22	16738.22	1.00	1.14	1.14	1.14	69	61.2
4-Aug-15	8:10	Fine	012728	2.8406	2.8552	16786.23	16787.23	1.00	1.14	1.14	1.14	68	213.7
4-Aug-15	9:13	Fine	012731	2.8593	2.8715	16787.23	16788.23	1.00	1.14	1.14	1.14	68	178.6
4-Aug-15	10:16	Fine	012454	2.8304	2.8372	16788.23	16789.23	1.00	1.14	1.14	1.14	68	99.5
10-Aug-15	9:07	Fine	012804	2.8052	2.8168	6813.23	6814.23	1.00	1.23	1.23	1.23	74	157.7
10-Aug-15	10:18	Fine	012013	2.7997	2.8120	6814.23	6815.23	1.00	1.23	1.23	1.23	74	167.3
10-Aug-15	13:00	Fine	012806	2.8237	2.8328	6815.23	6816.23	1.00	1.23	1.23	1.23	74	123.7
15-Aug-15	8:05	Rainy	012405	2.8182	2.8277	6840.23	6841.23	1.00	1.23	1.23	1.23	74	128.8
15-Aug-15	9:08	Rainy	012665	2.8229	2.8364	6841.23	6842.23	1.00	1.23	1.23	1.23	74	183.0
15-Aug-15	10:15	Rainy	012664	2.8077	2.8208	6842.23	6843.23	1.00	1.23	1.23	1.23	74	177.6
21-Aug-15	10:15	Cloudy	013038	2.8004	2.8133	6867.34	6868.34	1.00	1.22	1.22	1.22	73	176.1
21-Aug-15	13:00	Cloudy	013033	2.8194	2.8333	6868.34	6869.34	1.00	1.22	1.22	1.22	73	189.8
21-Aug-15	14:05	Cloudy	013031	2.7924	2.8157	6869.35	6870.35	1.00	1.22	1.22	1.22	73	318.1
27-Aug-15	8:00	Cloudy	012983	2.7980	2.8130	6870.35	6871.35	1.00	1.23	1.23	1.23	74	204.0
27-Aug-15	9:58	Cloudy	013027	2.8037	2.8188	6871.82	6872.82	1.00	1.23	1.23	1.23	74	205.3
27-Aug-15	11:00	Cloudy	013024	2.8359	2.8493	6872.82	6873.82	1.00	1.23	1.23	1.23	74	182.2

Location: CMA2a - Causeway Bay Community Centre

Report on 24-hour TSP monitoring  
Action Level ( $\mu\text{g}/\text{m}^3$ ) - 169.5  
Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
28-Jul-15	8:00	Fine	012739	2.8188	2.8785	16385.96	16409.96	24.00	1.20	1.21	1.21	1735	34.4
3-Aug-15	8:00	Fine	012792	2.8163	2.9108	16412.96	16436.96	24.00	1.20	1.20	1.20	1732	54.6
8-Aug-15	8:00	Fine	012456	2.8197	3.0110	16439.96	16463.96	24.00	1.18	1.18	1.18	1704	112.3
14-Aug-15	8:00	Cloudy	012011	2.8297	2.9172	16466.95	16490.95	24.00	1.19	1.19	1.19	1718	50.9
20-Aug-15	8:00	Cloudy	012407	2.8020	2.9513	16493.95	16517.95	24.00	1.19	1.19	1.19	1711	87.3
26-Aug-15	8:00	Cloudy	013002	2.8000	3.1742	16520.95	16544.95	24.00	1.19	1.19	1.19	1714	218.3

Report on 1-hour TSP monitoring  
Action Level ( $\mu\text{g}/\text{m}^3$ ) - 323.4  
Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
29-Jul-15	8:02	Fine	012800	2.8132	2.8183	16409.96	16410.96	1.00	1.16	1.16	1.16	70	73.2
29-Jul-15	9:05	Fine	012797	2.8488	2.8592	16410.96	16411.96	1.00	1.16	1.16	1.16	70	149.3
29-Jul-15	10:10	Fine	012795	2.8332	2.8362	16411.96	16412.96	1.00	1.16	1.16	1.16	70	43.1
4-Aug-15	8:05	Fine	012729	2.8391	2.8440	16436.96	16437.96	1.00	1.16	1.16	1.16	69	70.5
4-Aug-15	9:08	Fine	012732	2.8327	2.8356	16437.96	16438.96	1.00	1.16	1.16	1.16	69	41.7
4-Aug-15	10:11	Fine	012734	2.8344	2.8443	16438.96	16439.96	1.00	1.16	1.16	1.16	69	142.5
10-Aug-15	9:22	Fine	012805	2.8228	2.8293	16463.96	16464.96	1.00	1.28	1.28	1.28	77	84.8
10-Aug-15	10:30	Fine	012014	2.8356	2.8412	16464.96	16465.96	1.00	1.28	1.28	1.28	77	73.0
10-Aug-15	13:00	Fine	012012	2.8331	2.8413	16465.96	16466.96	1.00	1.28	1.28	1.28	77	106.9
15-Aug-15	8:02	Rainy	012419	2.8140	2.8157	16490.95	16491.95	1.00	1.19	1.19	1.19	72	23.7
15-Aug-15	9:05	Rainy	012386	2.8114	2.8146	16491.95	16492.95	1.00	1.19	1.19	1.19	72	44.7
15-Aug-15	10:10	Rainy	012416	2.8386	2.8457	16492.95	16493.95	1.00	1.19	1.19	1.19	72	99.2
21-Aug-15	10:04	Cloudy	013039	2.8314	2.8384	16517.95	16518.95	1.00	1.19	1.19	1.19	71	98.3
21-Aug-15	13:00	Cloudy	013034	2.8226	2.8275	16518.95	16519.95	1.00	1.19	1.19	1.19	71	68.8
21-Aug-15	14:05	Cloudy	013032	2.8057	2.8208	16519.95	16520.95	1.00	1.19	1.19	1.19	71	212.1
27-Aug-15	9:56	Cloudy	013048	2.8435	2.8707	16544.95	16545.95	1.00	1.19	1.19	1.19	71	380.9
27-Aug-15	11:00	Cloudy	013045	2.8235	2.8458	16545.95	16546.95	1.00	1.19	1.19	1.19	71	312.3
27-Aug-15	14:00	Cloudy	012998	2.9015	2.9265	16546.95	16547.95	1.00	1.19	1.19	1.19	71	350.1



Location: CMA3a - CWB PRE Site Office Area

Report on 24-hour TSP monitoring  
Action Level ( $\mu\text{g}/\text{m}^3$ ) - 171  
Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
28-Jul-15	8:00	Fine	011601	2.7373	2.8150	3845.25	3869.25	24.00	1.18	1.18	1.18	1702	45.7
3-Aug-15	8:00	Fine	012819	2.8766	2.9965	3872.24	3896.24	24.00	1.18	1.18	1.18	1697	70.6
8-Aug-15	8:00	Fine	012837	2.8338	2.9840	3899.24	3923.24	24.00	1.23	1.23	1.23	1774	84.7
14-Aug-15	8:00	Cloudy	012679	2.8376	2.9689	3926.24	3950.24	24.00	1.20	1.20	1.20	1722	76.3
20-Aug-15	8:00	Cloudy	012660	2.8013	3.0704	3953.24	3977.24	24.00	1.19	1.19	1.19	1714	157.0
26-Aug-15	8:00	Cloudy	012984	2.7982	2.9095	3980.26	4004.26	24.00	1.19	1.19	1.19	1718	64.8

Report on 1-hour TSP monitoring  
Action Level ( $\mu\text{g}/\text{m}^3$ ) - 311.3  
Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
29-Jul-15	9:27	Fine	012799	2.8181	2.8245	3869.25	3870.25	1.00	1.20	1.20	1.20	72	88.6
29-Jul-15	10:32	Fine	012031	2.8367	2.8422	3870.25	3871.25	1.00	1.20	1.20	1.20	72	76.1
29-Jul-15	13:00	Fine	012799	2.8181	2.8227	3871.25	3872.25	1.00	1.20	1.20	1.20	72	63.7
4-Aug-15	8:42	Fine	012831	2.8743	2.8785	3896.24	3897.24	1.00	1.20	1.20	1.20	72	58.4
4-Aug-15	9:45	Fine	012834	2.8725	2.8776	3897.24	3898.24	1.00	1.20	1.20	1.20	72	70.9
4-Aug-15	10:48	Fine	012835	2.8609	2.8663	3898.24	3899.24	1.00	1.20	1.20	1.20	72	75.0
10-Aug-15	8:30	Fine	012839	2.8540	2.8605	3923.24	3924.24	1.00	1.29	1.29	1.29	77	84.0
10-Aug-15	9:47	Fine	012841	2.8367	2.8402	3924.24	3925.24	1.00	1.29	1.29	1.29	77	45.2
10-Aug-15	13:00	Fine	012027	2.8347	2.8416	3925.24	3926.24	1.00	1.29	1.29	1.29	77	89.1
15-Aug-15	8:10	Rainy	012404	2.8198	2.8281	3950.24	3951.24	1.00	1.24	1.24	1.24	74	111.5
15-Aug-15	9:23	Rainy	012669	2.8292	2.8345	3951.24	3952.24	1.00	1.24	1.24	1.24	74	71.2
15-Aug-15	10:26	Rainy	012663	2.8305	2.8401	3952.24	3953.24	1.00	1.24	1.24	1.24	74	128.9
21-Aug-15	9:25	Cloudy	013040	2.8331	2.8387	3977.24	3978.24	1.00	1.23	1.23	1.23	74	75.7
21-Aug-15	11:00	Cloudy	013035	2.8011	2.8091	3978.24	3979.24	1.00	1.23	1.23	1.23	74	108.2
21-Aug-15	14:35	Cloudy	013005	2.7824	2.7911	3979.24	3980.24	1.00	1.23	1.23	1.23	74	117.6
27-Aug-15	9:45	Cloudy	013049	2.8094	2.8175	4004.26	4005.26	1.00	1.24	1.24	1.24	74	109.1
27-Aug-15	10:50	Cloudy	013025	2.7993	2.8092	4005.26	4006.26	1.00	1.24	1.24	1.24	74	133.4
27-Aug-15	13:00	Cloudy	013023	2.8120	2.8230	4006.26	4007.26	1.00	1.24	1.24	1.24	74	148.2

Location: CMA4a - SPCA

Report on 24-hour TSP monitoring  
Action Level ( $\mu\text{g}/\text{m}^3$ ) - 171.2  
Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
28-Jul-15	8:00	Fine	011602	2.7299	2.8133	20659.90	20683.90	24.00	1.23	1.24	1.23	1778	46.9
3-Aug-15	8:00	Fine	012803	2.8244	2.9195	20686.89	20710.89	24.00	1.23	1.23	1.23	1774	53.6
8-Aug-15	8:00	Fine	012836	2.8538	3.1005	20713.89	20737.89	24.00	1.23	1.23	1.23	1774	139.1
14-Aug-15	8:00	Cloudy	012680	2.8358	3.0324	20740.89	20764.89	24.00	1.15	1.15	1.15	1654	118.9
20-Aug-15	8:00	Cloudy	012406	2.8137	3.0565	20767.89	20791.89	24.00	1.24	1.24	1.24	1782	136.3
26-Aug-15	8:00	Cloudy	013003	2.8097	2.9403	20794.89	20818.89	24.00	1.24	1.24	1.24	1786	73.1

Report on 1-hour TSP monitoring  
Action Level ( $\mu\text{g}/\text{m}^3$ ) - 312.5  
Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
29-Jul-15	9:07	Fine	012028	2.8507	2.8579	20683.90	20684.90	1.00	1.24	1.24	1.24	74	97.1
29-Jul-15	10:17	Fine	012801	2.8111	2.8224	20684.90	20685.90	1.00	1.24	1.24	1.24	74	152.4
29-Jul-15	13:00	Fine	012029	2.8311	2.8362	20685.90	20686.90	1.00	1.24	1.24	1.24	74	68.8
4-Aug-15	8:25	Fine	012745	2.8463	2.8508	20710.89	20711.89	1.00	1.23	1.23	1.23	74	60.9
4-Aug-15	9:29	Fine	012832	2.8437	2.8477	20711.89	20712.89	1.00	1.23	1.23	1.23	74	54.1
4-Aug-15	10:36	Fine	012833	2.8601	2.8650	20712.89	20713.89	1.00	1.23	1.23	1.23	74	66.3
10-Aug-15	8:10	Fine	012838	2.8392	2.8485	20737.89	20738.89	1.00	1.24	1.24	1.24	74	125.0
10-Aug-15	10:00	Fine	012840	2.8585	2.8649	20738.89	20739.89	1.00	1.24	1.24	1.24	74	86.0
10-Aug-15	13:00	Fine	012802	2.8199	2.8275	20739.89	20740.89	1.00	1.24	1.24	1.24	74	102.1
15-Aug-15	8:02	Rainy	012674	2.8490	2.8518	20764.89	20765.89	1.00	1.24	1.24	1.24	75	37.5
15-Aug-15	9:16	Rainy	012670	2.8147	2.8186	20765.89	20766.89	1.00	1.24	1.24	1.24	75	52.3
15-Aug-15	10:26	Rainy	012415	2.8351	2.8425	20766.89	20767.89	1.00	1.24	1.24	1.24	75	99.2
21-Aug-15	9:15	Cloudy	013041	2.7930	2.8052	20791.89	20792.89	1.00	1.24	1.24	1.24	74	164.6
21-Aug-15	13:00	Cloudy	013036	2.8037	2.8155	20792.89	20793.89	1.00	1.24	1.24	1.24	74	159.2
21-Aug-15	14:27	Cloudy	013006	2.7901	2.8132	20793.89	20794.89	1.00	1.24	1.24	1.24	74	311.6
27-Aug-15	9:37	Cloudy	013000	2.8060	2.8159	20818.89	20819.89	1.00	1.24	1.24	1.24	74	133.1
27-Aug-15	10:50	Cloudy	013046	2.7985	2.8101	20819.89	20820.89	1.00	1.24	1.24	1.24	74	155.9
27-Aug-15	13:00	Cloudy	012996	2.8159	2.8272	20820.89	20821.89	1.00	1.24	1.24	1.24	74	151.9



Location: CMA5b - Pedestrian Plaza

Report on 24-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 181  
Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 260

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
28-Jul-15	8:00	Fine	012725	2.8283	3.0003	5146.87	5170.87	24.00	1.01	1.01	1.01	1460	117.8
3-Aug-15	8:00	Fine	012741	2.8125	2.9499	5197.89	5221.89	24.00	1.03	1.03	1.03	1477	93.0
8-Aug-15	8:00	Fine	012750	2.8281	3.0357	5224.89	5248.89	24.00	1.02	1.02	1.02	1465	141.7
14-Aug-15	8:00	Cloudy	012457	2.8115	2.8813	5251.88	5275.88	24.00	0.98	0.98	0.98	1406	49.7
20-Aug-15	8:00	Cloudy	012658	2.8185	2.9836	5278.88	5302.88	24.00	0.97	0.97	0.97	1397	118.2
26-Aug-15	8:00	Cloudy	013004	2.7839	2.8707	5305.88	5329.88	24.00	0.97	0.97	0.97	1401	61.9

Report on 1-hour TSP monitoring

Action Level ( $\mu\text{g}/\text{m}^3$ ) - 332  
Limit Level ( $\mu\text{g}/\text{m}^3$ ) - 500

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
29-Jul-15	13:00	Fine	012427	2.7979	2.8082	5194.89	5195.89	1.00	0.96	0.96	0.96	58	178.4
29-Jul-15	14:04	Fine	012825	2.8779	2.8853	5195.89	5196.89	1.00	0.96	0.96	0.96	58	128.2
29-Jul-15	15:16	Fine	012828	2.8761	2.8823	5196.89	5197.89	1.00	0.96	0.96	0.96	58	107.4
4-Aug-15	13:00	Fine	012460	2.7991	2.8060	5221.89	5222.89	1.00	1.03	1.03	1.03	62	112.1
4-Aug-15	14:16	Fine	012682	2.8420	2.8473	5222.89	5223.89	1.00	1.03	1.03	1.03	62	86.1
4-Aug-15	15:20	Fine	012747	2.8424	2.8490	5223.89	5224.89	1.00	1.03	1.03	1.03	62	107.2
10-Aug-15	9:15	Fine	012453	2.8273	2.8356	5248.89	5249.89	1.00	1.03	1.03	1.03	62	134.8
10-Aug-15	10:35	Fine	012753	2.8457	2.8506	5249.89	5250.89	1.00	1.03	1.03	1.03	62	79.6
10-Aug-15	13:00	Fine	012666	2.8320	2.8360	5250.89	5251.89	1.00	1.03	1.03	1.03	62	65.0
15-Aug-15	8:13	Rainy	012673	2.8544	2.8552	5275.88	5276.88	1.00	0.98	0.98	0.98	59	13.7
15-Aug-15	9:16	Rainy	012668	2.8315	2.8323	5276.88	5277.88	1.00	0.98	0.98	0.98	59	13.7
15-Aug-15	10:37	Rainy	012414	2.8242	2.8304	5277.88	5278.88	1.00	1.03	1.03	1.03	62	100.3
21-Aug-15	8:32	Cloudy	013042	2.8110	2.8198	5302.88	5303.88	1.00	0.97	0.97	0.97	58	151.4
21-Aug-15	10:52	Cloudy	013037	2.7899	2.7994	5303.88	5304.88	1.00	0.97	0.97	0.97	58	163.5
21-Aug-15	14:00	Cloudy	013029	2.7859	2.8016	5304.88	5305.88	1.00	0.97	0.97	0.97	58	270.2
27-Aug-15	8:47	Cloudy	013001	2.8017	2.8094	5329.88	5330.88	1.00	0.97	0.97	0.97	58	131.9
27-Aug-15	10:25	Cloudy	013047	2.8138	2.8220	5330.88	5331.88	1.00	1.03	1.08	1.05	63	129.9
27-Aug-15	13:11	Cloudy	012970	2.8022	2.8094	5331.88	5332.88	1.00	0.97	0.97	0.97	58	123.3



Location: CMA6a - WD2 PRE Office

Report on 24-hour TSP monitoring

Action Level - 187.3  $\mu\text{g}/\text{m}^3$   
Limit Level - 260  $\mu\text{g}/\text{m}^3$

Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
28-Jul-15	8:00	Fine	012724	2.8415	2.9530	20242.62	20266.62	24.00	1.22	1.22	1.22	1762	63.3
3-Aug-15	8:00	Fine	012829	2.8823	3.0403	20269.63	20293.63	24.00	1.22	1.22	1.22	1757	89.9
8-Aug-15	8:00	Fine	012748	2.8252	3.0363	20296.64	20320.64	24.00	1.20	1.20	1.20	1731	121.9
14-Aug-15	8:00	Cloudy	012667	2.8266	2.9928	20323.64	20347.64	24.00	1.22	1.22	1.22	1751	94.9
20-Aug-15	8:00	Cloudy	012661	2.8113	3.0911	20350.64	20374.64	24.00	1.21	1.21	1.21	1741	160.7
29-Aug-15	11:30	Cloudy	012657	2.8123	2.9420	20380.65	20404.65	24.00	1.21	1.22	1.21	1749	74.2

Remarks: Due to interruption of electricity, the 24hr TSP was rescheduled from 26 August 2015 to 29 August 2015.




Report on 1-hour TSP monitoring

Action Level - 300.1  $\mu\text{g}/\text{m}^3$   
Limit Level - 500  $\mu\text{g}/\text{m}^3$




Date	Sampling Time	Weather Condition	Filter paper no.	Filter Weight, g		Elapse Time, hr		Sampling Time, hr	Flow Rate, $\text{m}^3/\text{min}$			Total Volume, $\text{m}^3$	TSP Level, $\mu\text{g}/\text{m}^3$
				Initial	Final	Initial	Final		Initial, $Q_{si}$	Final, $Q_{sf}$	Average		
29-Jul-15	13:00	Fine	012429	2.8080	2.8171	20266.63	20267.63	1.00	1.22	1.22	1.22	73	123.9
29-Jul-15	14:06	Fine	012426	2.8149	2.8247	20267.63	20268.63	1.00	1.22	1.22	1.22	73	133.4
29-Jul-15	15:10	Fine	012826	2.8706	2.8757	20268.63	20269.63	1.00	1.22	1.22	1.22	73	69.4
4-Aug-15	13:00	Fine	012462	2.8144	2.8198	20293.63	20294.63	1.00	1.22	1.22	1.22	73	73.8
4-Aug-15	14:05	Fine	012684	2.8364	2.8442	20294.63	20295.63	1.00	1.22	1.22	1.22	73	106.5
4-Aug-15	15:08	Fine	012681	2.8410	2.8481	20295.64	20296.64	1.00	1.22	1.22	1.22	73	97.0
10-Aug-15	9:15	Fine	012752	2.8384	2.8523	20320.64	20321.64	1.00	1.21	1.21	1.21	73	191.1
10-Aug-15	10:50	Fine	012459	2.8053	2.8095	20321.64	20322.64	1.00	1.21	1.21	1.21	73	57.7
10-Aug-15	13:00	Fine	012655	2.8050	2.8212	20322.65	20323.65	1.00	1.21	1.21	1.21	73	222.7
15-Aug-15	8:23	Rainy	012672	2.8410	2.8452	20347.64	20348.64	1.00	1.22	1.22	1.22	73	57.5
15-Aug-15	9:41	Rainy	012418	2.8306	2.8390	20348.64	20349.64	1.00	1.22	1.22	1.22	73	115.0
15-Aug-15	10:45	Rainy	012413	2.8186	2.8235	20349.64	20350.64	1.00	1.22	1.22	1.22	73	67.1
21-Aug-15	8:12	Cloudy	013043	2.8023	2.8149	20374.64	20375.64	1.00	1.21	1.21	1.21	72	174.0
21-Aug-15	10:36	Cloudy	012987	2.7938	2.8064	20375.64	20376.64	1.00	1.21	1.21	1.21	72	174.0
21-Aug-15	13:00	Cloudy	012985	2.8046	2.8204	20376.65	20377.65	1.00	1.21	1.21	1.21	72	218.2
27-Aug-15	16:00	Cloudy	013044	2.7995	2.8092	20377.65	20378.65	1.00	1.21	1.21	1.21	73	133.3
27-Aug-15	17:14	Cloudy	012995	2.8186	2.8283	20378.65	20379.65	1.00	1.21	1.21	1.21	73	133.3
28-Aug-15	8:57	Cloudy	012994	2.8066	2.8194	20379.65	20380.65	1.00	1.21	1.21	1.21	73	175.8

Remarks: Due to interruption of electricity, the 1hr TSP was rescheduled from 27 August 2015 to 28 August 2015.

Graphic Presentation of 1 hour TSP Result

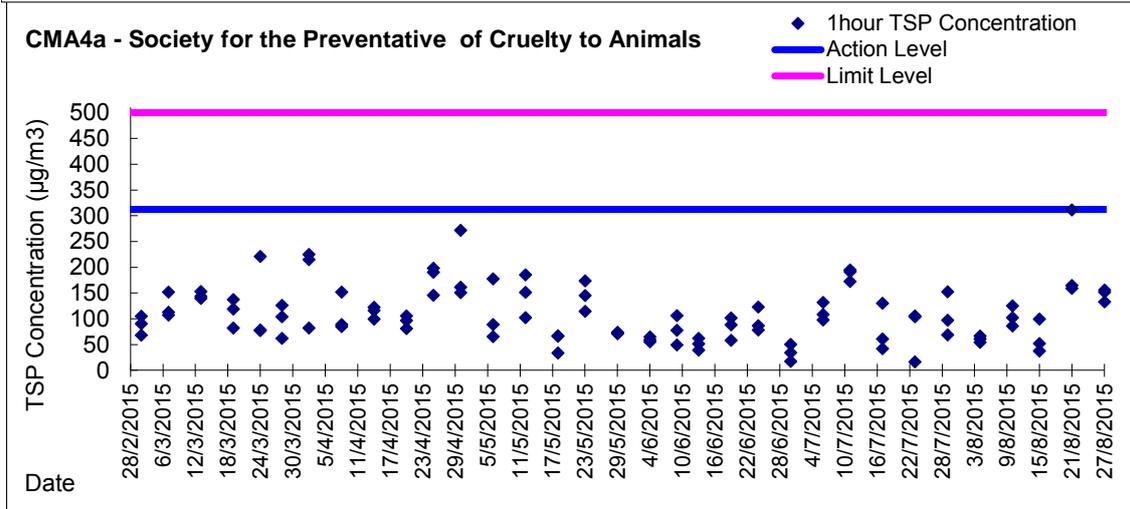
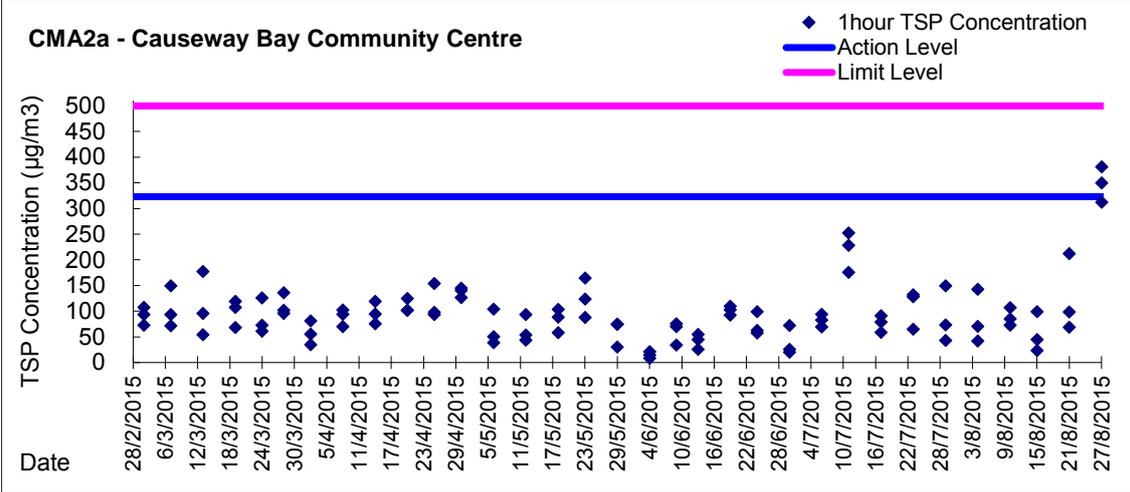
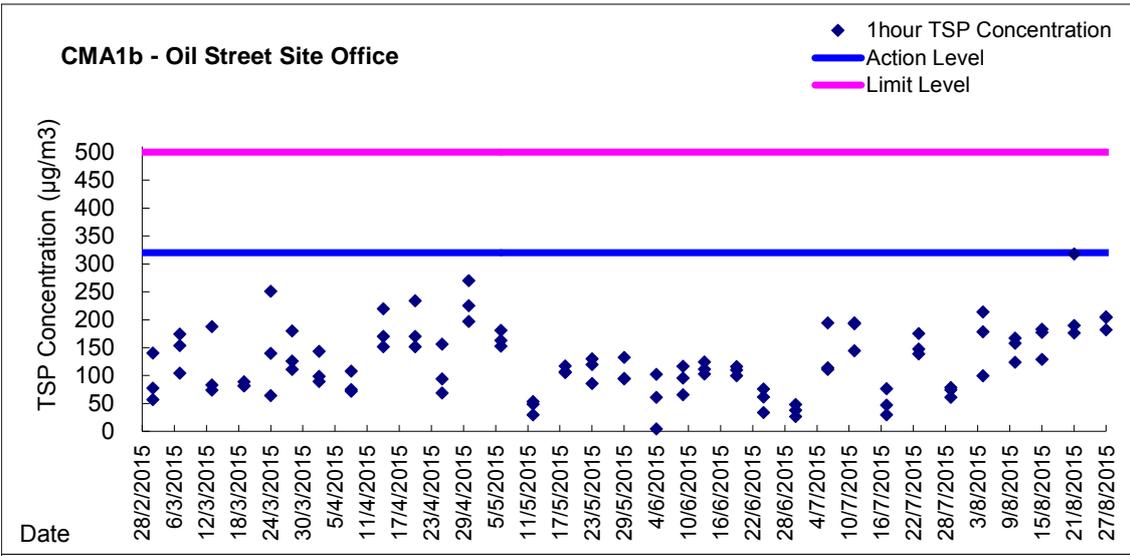


Graphic Presentation of 1 hour TSP Result

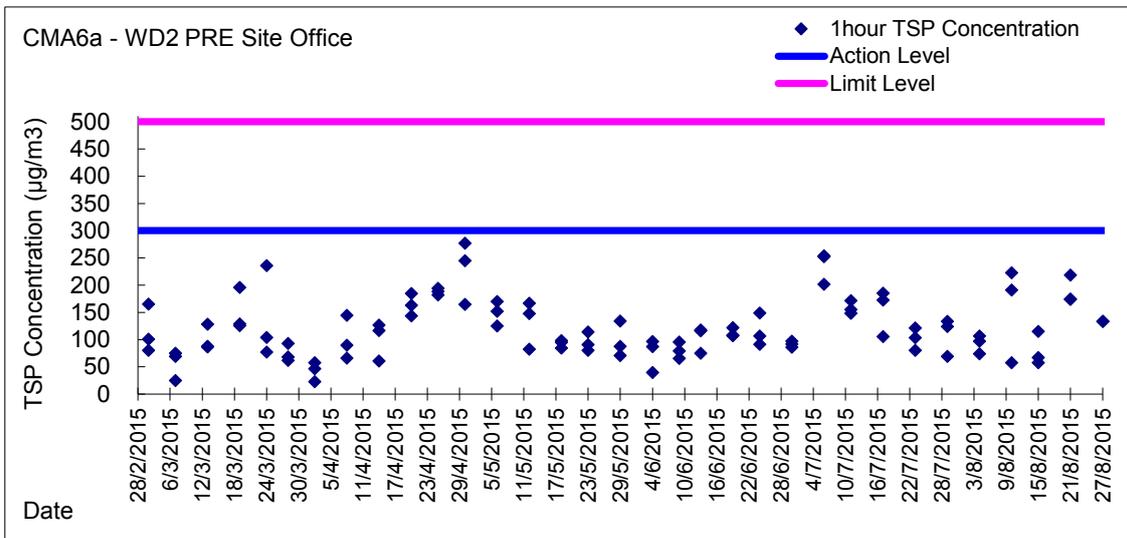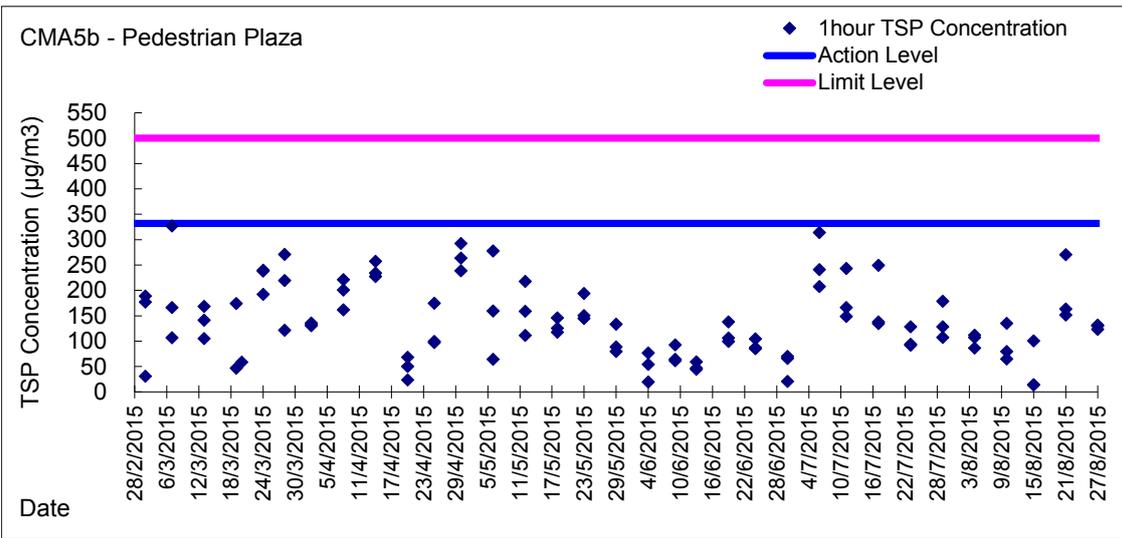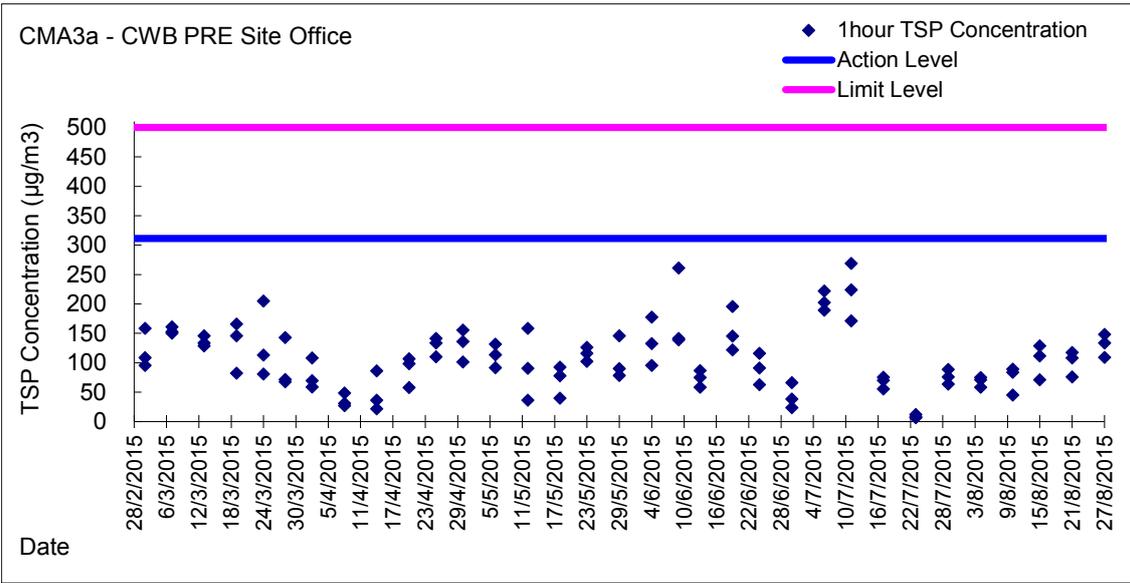






Graphic Presentation of 24 hour TSP Result

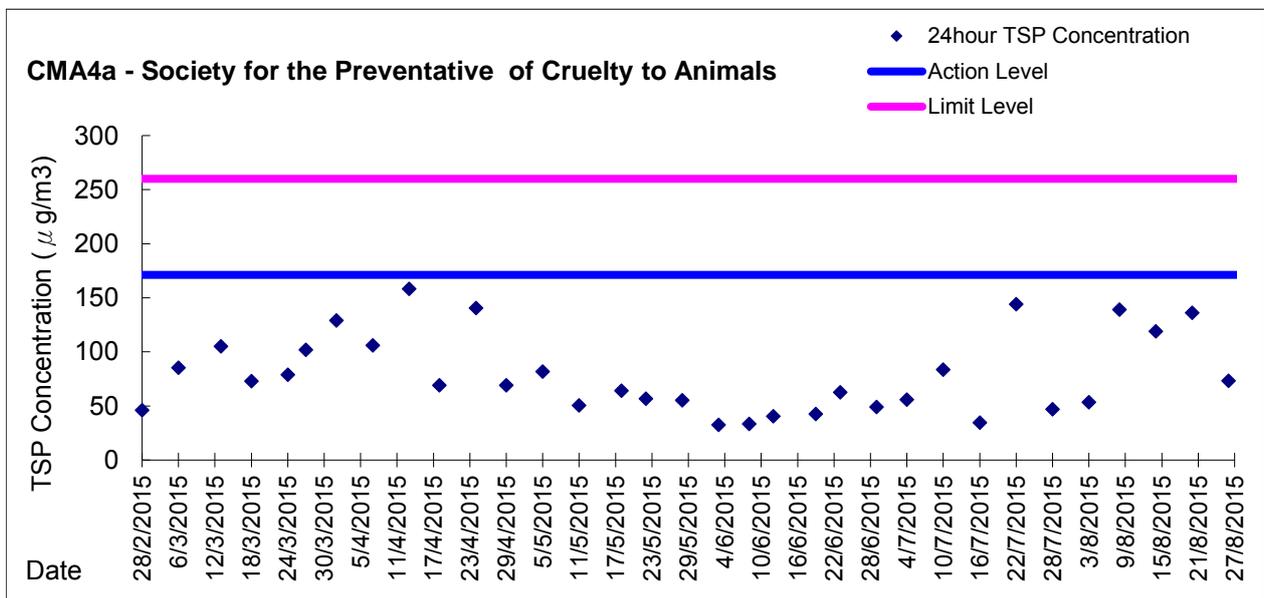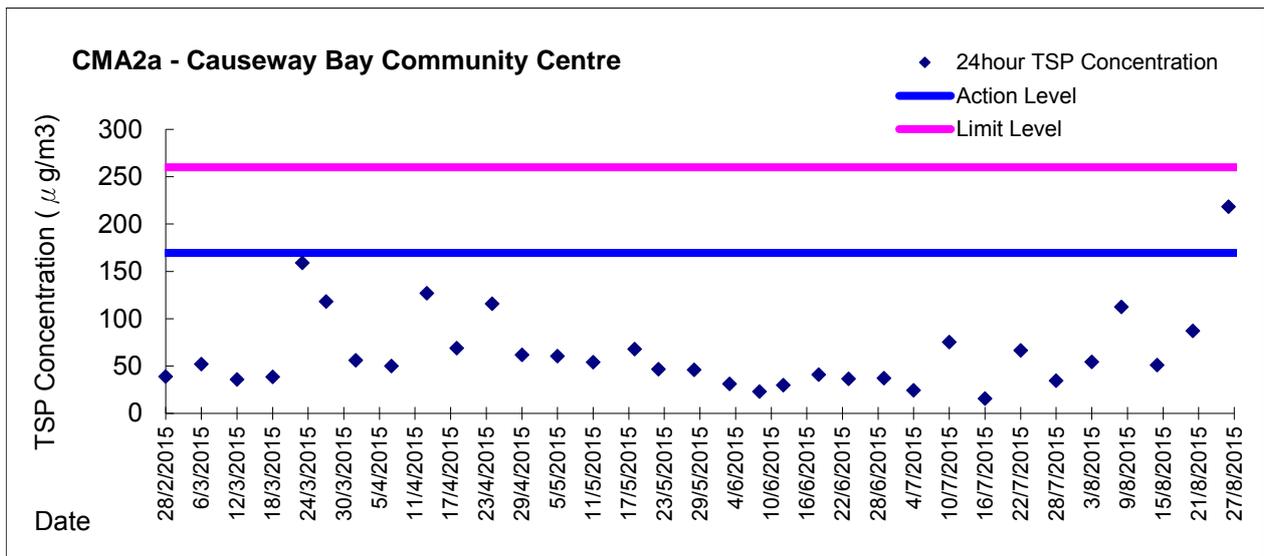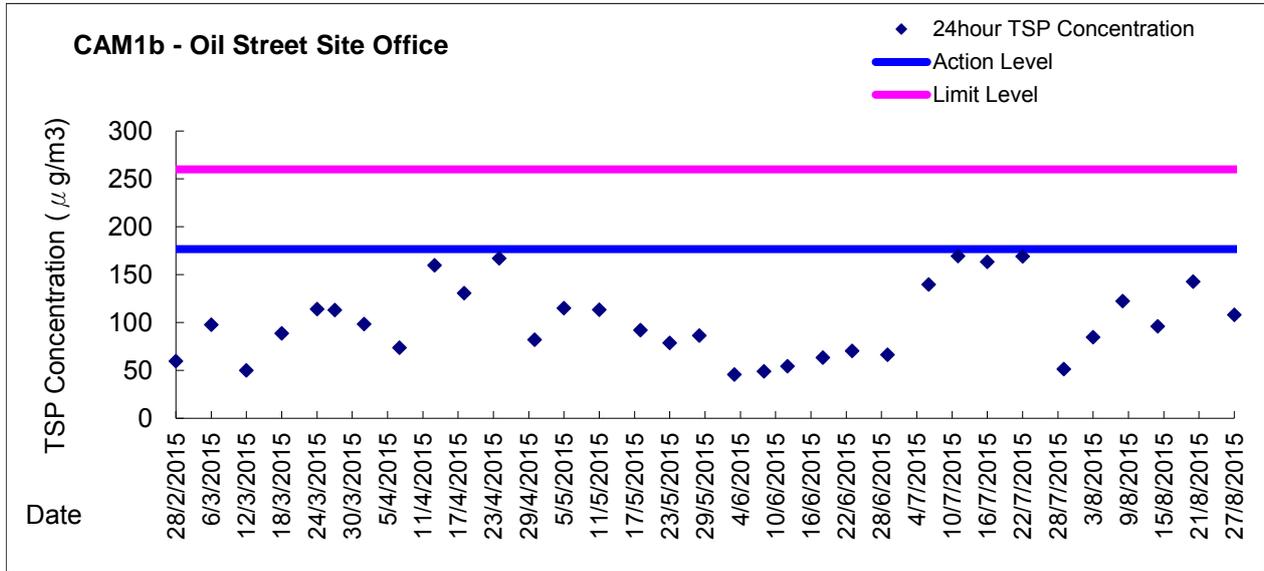



Graphic Presentation of 24 hour TSP Result

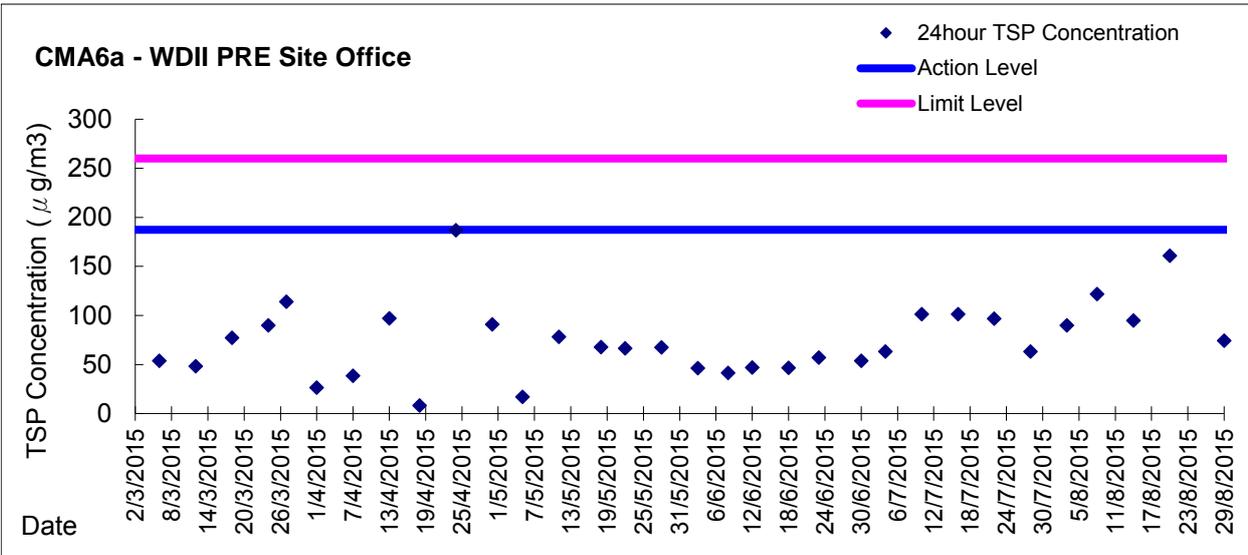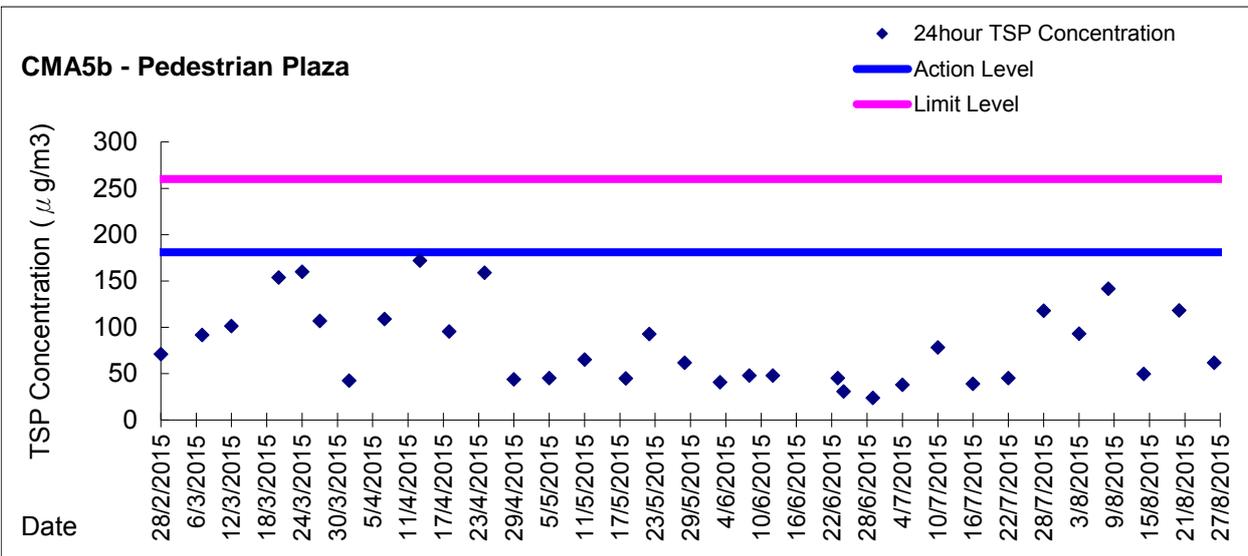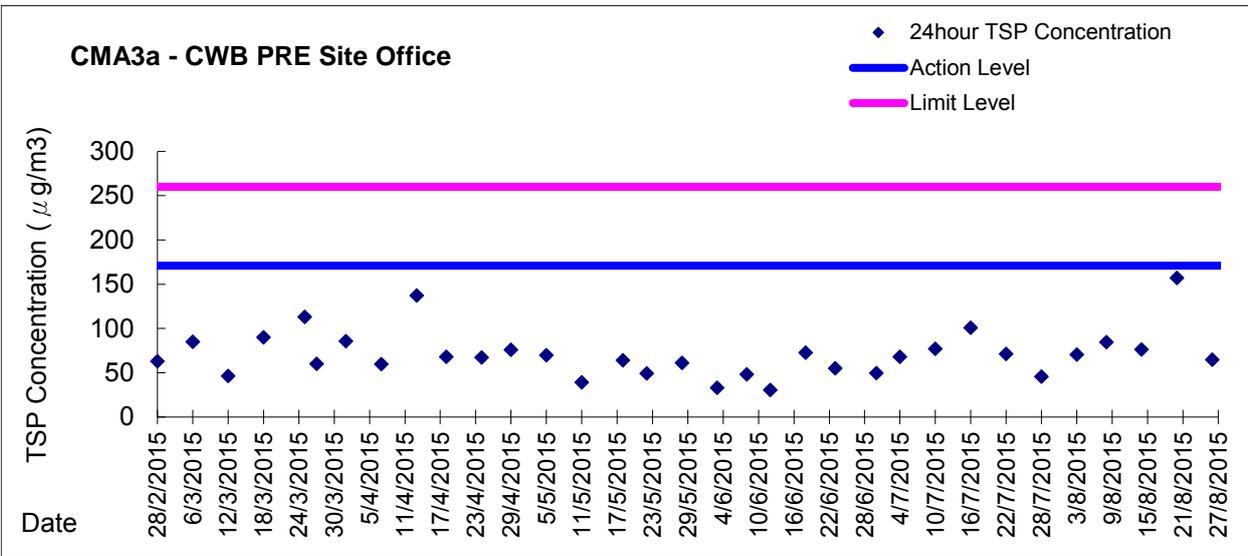



**Field Data Record Sheet**

Monitoring Date: 4 August 2015  
Temperature: 30.0°C – 37.4°C

Weather Condition: Fine  
Relative Humidity: 50.9% - 74.1%

Tidal Condition: Ebb

Location	Time	Temperature (°C)	Relative Humidity (%)	Odour Intensity	Odour Nature	Possible Odour Sources	Duration	Wind Speed(m/s)	Wind Direction	Remarks
OP7	13:50	30.0	74.1	0-1	Sewage	Sea	Persistent	0.8	NNW	
OP6	13:55	31.8	50.9	0-1	Seawater	Sea	Persistent	0.7	NNW	
OP5	14:00	30.8	70.0	1	Sewage	Sea	Intermittent	0.6	WNW	
OP4	14:05	32.5	68.8	0-1	Sewage	Sea	Intermittent	0.6	NNE	
OP3	14:10	34.7	63.8	0	/	/	/	0.7	ESE	
OP2	14:15	34.8	63.8	0-1	Sewage	Sea	Intermittent	0.6	N	
OP1	14:20	37.4	57.7	1	Sewage	Sea	Persistent	0.5	NNE	


Remarks for Odour Intensity: The perceived odour intensity is to be divided into 5 levels which are ranked in the descending order as follows:  
 0 – Not detected. No odour perceived or an odour so weak that it cannot be easily characterised or described;  
 1 – Slight Identifiable odour, and slight chance to have odour nuisance;  
 2 – Moderate Identifiable odour, and moderate chance to have odour nuisance  
 3 – Strong Identifiable, likely to have odour nuisance;  
 4 – Extreme Severe odour, and unacceptable level



**Meteorological Conditions on 4 August 2015**

- **Hong Kong Observatory Weather Station at Hong Kong Observatory**  
Air Temperature: 26.8 – 33.3 °C      Relative humidity: 59 – 90%
- **Hong Kong Observatory Weather Station at Hong Kong Park**  
Air Temperature: 25.9 – 32.5 °C
- **The tidal data at Quarry Bay Station**

Tide Time	Tide Height (m)
00:42	1.7
05:24	0.9
12:05	2.2
18:12	0.6

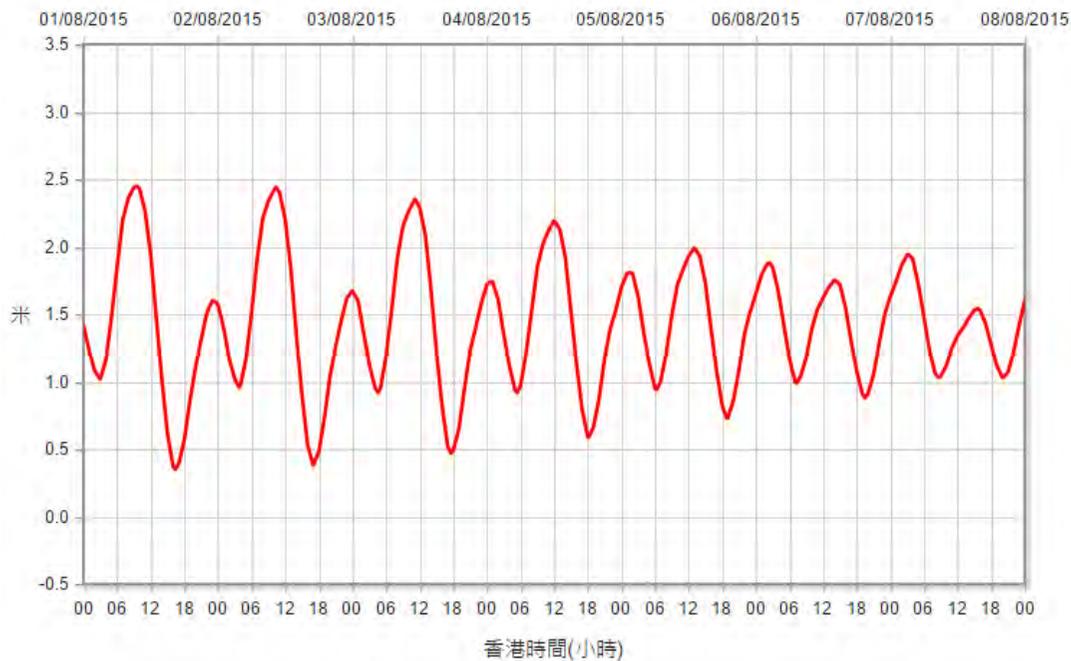



**Field Data Record Sheet**

Monitoring 18 August 2015  
Date:  
Temperature: 32.0°C – 36.7°C

Weather Condition: Fine  
Relative Humidity: 57.7% - 73.8%

Tidal Condition: Ebb

Location	Time	Temperature (°C)	Relative Humidity (%)	Odour Intensity	Odour Nature	Possible Odour Sources	Duration	Wind Speed(m/s)	Wind Direction	Remarks
OP7	13:24	32.0	73.8	0-1	Seawater	Sea	Intermittent	1.0	WNW	
OP6	13:30	34.5	66.0	0	/	/	/	1.2	WNW	
OP5	13:36	33.9	67.4	0-1	Culvert discharge	Sea	Intermittent	2.0	WNW	
OP4	13:42	36.3	57.7	0	/	/	/	0.7	NW	
OP3	13:48	32.6	67.6	0	/	/	/	2.5	NW	
OP2	13:55	36.7	58.6	0-1	Culvert discharge	Sea	Intermittent	1.9	W	
OP1	13:58	33.7	65.2	1	Culvert discharge	Sea	Intermittent	1.2	NNE	


Remarks for Odour Intensity: The perceived odour intensity is to be divided into 5 levels which are ranked in the descending order as follows:  
 0 – Not detected. No odour perceived or an odour so weak that it cannot be easily characterised or described;  
 1 – Slight Identifiable odour, and slight chance to have odour nuisance;  
 2 – Moderate Identifiable odour, and moderate chance to have odour nuisance  
 3 – Strong Identifiable, likely to have odour nuisance;  
 4 – Extreme Severe odour, and unacceptable level



**Meteorological Conditions on 18 August 2015**

- **Hong Kong Observatory Weather Station at Hong Kong Observatory**  
Air Temperature: 28.4 – 33.8 °C      Relative humidity: 65 – 89%
- **Hong Kong Observatory Weather Station at Hong Kong Park**  
Air Temperature: 28.6 – 32.4 °C
- **The tidal data at Quarry Bay Station**

Tide Time	Tide Height (m)
03:41	1.1
10:26	2.2
17:20	0.4

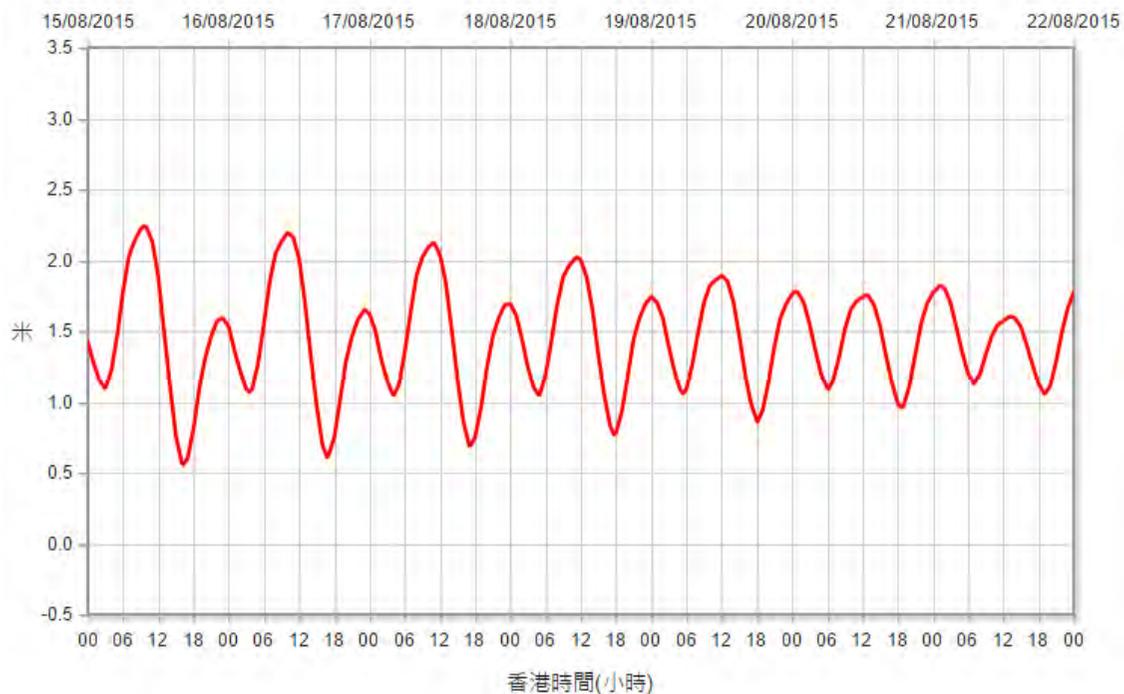



***Appendix 5.4***

***Water Quality and Additional Dissolved Oxygen Monitoring Results and Graphical Presentations***



**Water Monitoring Result at C7 - Windsor House  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth m	Water Temperature °C			pH		Salinity ppt		DO Saturation %		DO mg/L		Turbidity NTU		Suspended Solids mg/L							
				Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average							
28/7/2015	-	Fine	Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-						
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-						
30/7/2015	18:35	Cloudy	Middle	-	27.40	27.40	27.40	8.23	8.23	8.27	26.68	26.68	26.68	87.8	88.5	88.3	5.98	6.03	6.02	2.04	2.01	2.01	3	3.00
	18:37		Middle	-	27.40	27.40	27.40	8.30	8.30	8.27	26.67	26.67	26.68	88.5	88.4	88.3	6.03	6.02	6.02	2.00	2.00	2.01	3	3.00
1/8/2015	21:32	Fine	Middle	-	25.93	25.93	25.94	7.58	7.58	7.58	27.20	27.20	27.19	88.3	88.1	88.0	6.26	6.25	6.24	1.98	1.78	1.84	3	3.50
	21:33		Middle	-	25.94	25.94	25.94	7.57	7.57	7.58	27.18	27.18	27.19	87.8	87.9	88.0	6.22	6.24	6.24	1.76	1.83	1.84	4	3.50
3/8/2015	19:38	Fine	Middle	-	27.40	27.40	27.45	7.46	7.46	7.46	29.02	29.02	29.00	91.9	91.7	91.4	6.18	6.16	6.14	1.15	1.09	1.05	2	2.00
	19:39		Middle	-	27.49	27.49	27.45	7.46	7.46	7.46	28.99	28.98	29.00	91.1	91.0	91.4	6.12	6.11	6.14	1.08	0.87	1.05	2	2.00
5/8/2015	10:43	Fine	Middle	-	27.20	27.20	27.25	8.23	8.23	8.22	29.75	29.75	29.76	73.9	72.9	72.7	4.91	4.90	4.87	2.21	2.21	2.23	4	4.00
	10:45		Middle	-	27.30	27.30	27.25	8.20	8.20	8.22	29.76	29.76	29.76	73.1	70.8	72.7	4.91	4.76	4.87	2.25	2.23	2.23	4	4.00
7/8/2015	12:45	Fine	Middle	-	28.10	28.10	28.15	8.21	8.21	8.22	29.56	29.56	29.57	86.4	85.9	85.8	5.72	5.69	5.68	2.96	2.81	2.83	3	2.50
	12:47		Middle	-	28.20	28.20	28.15	8.23	8.23	8.22	29.58	29.58	29.57	85.4	85.3	85.8	5.66	5.65	5.68	2.77	2.76	2.83	2	2.50
10/8/2015	13:30	Cloudy	Middle	-	27.70	27.70	27.75	8.33	8.33	8.32	30.38	30.38	30.38	81.7	81.3	81.2	5.40	5.40	5.39	6.12	6.36	6.24	3	3.50
	13:32		Middle	-	27.80	27.80	27.75	8.30	8.30	8.32	30.38	30.38	30.38	80.9	80.9	81.2	5.37	5.37	5.39	6.13	6.35	6.24	4	3.50
12/8/2015	15:15	Fine	Middle	-	28.40	28.40	28.65	8.23	8.23	8.21	31.03	31.03	31.03	74.5	73.4	73.7	4.85	4.78	4.79	2.51	2.51	2.47	6	6.50
	15:17		Middle	-	28.90	28.90	28.65	8.18	8.18	8.21	31.02	31.02	31.03	73.3	73.4	73.7	4.77	4.77	4.79	2.46	2.39	2.47	7	6.50
14/8/2015	18:27	Cloudy	Middle	-	26.00	26.00	26.05	8.40	8.40	8.39	29.87	29.87	29.87	75.2	76.5	75.3	5.20	5.23	5.16	3.26	3.44	3.32	4	4.00
	18:28		Middle	-	26.10	26.10	26.05	8.37	8.37	8.39	29.87	29.87	29.87	75.4	73.9	75.3	5.16	5.06	5.16	3.28	3.30	3.32	4	4.00
17/8/2015	10:35	Fine	Middle	-	26.60	26.60	26.55	8.12	8.12	8.12	30.40	30.40	30.40	70.4	69.8	69.4	4.75	4.71	4.74	2.87	2.87	2.85	5	4.50
	10:37		Middle	-	26.50	26.50	26.55	8.11	8.11	8.12	30.39	30.39	30.40	69.7	67.8	69.4	4.71	4.78	4.74	2.87	2.77	2.85	4	4.50
19/8/2015	9:49	Fine	Middle	-	26.90	26.90	26.95	8.08	8.08	8.09	30.37	30.37	30.37	62.6	63.0	63.5	4.21	4.24	4.27	8.52	8.62	8.55	9	8.50
	9:51		Middle	-	27.00	27.00	26.95	8.09	8.09	8.09	30.37	30.37	30.37	63.7	64.5	63.5	4.29	4.34	4.27	8.49	8.55	8.55	8	8.50
21/8/2015	11:22	Fine	Middle	-	28.30	28.30	28.25	8.07	8.07	8.08	31.05	31.05	31.06	67.0	66.6	66.3	4.40	4.35	4.35	2.30	2.33	2.36	3	3.00
	11:24		Middle	-	28.20	28.20	28.25	8.08	8.08	8.08	31.06	31.06	31.06	66.1	65.6	66.3	4.34	4.31	4.35	2.32	2.50	2.36	3	3.00
25/8/2015	17:00	Fine	Middle	-	27.60	27.60	27.75	8.23	8.23	8.23	32.16	32.16	32.15	74.9	76.0	75.9	4.92	4.99	4.98	2.75	2.74	2.74	7	6.00
	17:02		Middle	-	27.90	27.90	27.75	8.23	8.23	8.23	32.13	32.13	32.15	76.8	75.9	75.9	5.04	4.98	4.98	2.74	2.74	2.74	5	6.00
27/8/2015	17:50	Fine	Middle	-	27.20	27.20	27.25	8.19	8.19	8.20	32.47	32.47	32.47	72.9	73.8	73.7	4.82	4.88	4.87	3.76	3.76	3.81	6	5.00
	17:52		Middle	-	27.30	27.30	27.25	8.20	8.20	8.20	32.47	32.47	32.47	73.2	74.7	73.7	4.84	4.94	4.87	3.86	3.87	3.81	4	5.00

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at C1 - HKCEC Extension  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids						
					°C		-		ppt		%		mg/L		NTU		mg/L							
			m	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average					
28/7/2015	16:25	Fine	Middle	2.5	27.60	27.60	27.60	8.18	8.18	8.18	26.74	26.74	26.75	73.9	73.8	73.0	5.02	5.01	4.96	1.52	1.52	1.52	7	6.50
	16:27		Middle	2.5	27.60	27.60	27.60	8.18	8.18	8.18	26.75	26.75	26.75	71.5	72.8	73.0	4.85	4.94	4.96	1.51	1.52	1.52	6	
30/7/2015	16:57	Cloudy	Middle	2.5	26.40	26.40	26.40	8.33	8.33	8.33	27.81	27.81	27.82	65.0	64.0	64.0	4.48	4.41	4.36	3.94	3.97	3.92	8	8.00
	16:59		Middle	2.5	26.40	26.40	26.40	8.33	8.33	8.33	27.83	27.83	27.82	63.5	63.3	64.0	4.28	4.25	4.36	3.89	3.86	3.92	8	
1/8/2015	17:16	Fine	Middle	2.5	26.90	26.90	26.95	8.17	8.17	8.19	28.44	28.44	28.50	68.1	68.3	69.0	4.62	4.64	4.69	2.41	2.39	2.39	5	4.50
	17:18		Middle	2.5	27.00	27.00	26.95	8.20	8.20	8.19	28.56	28.56	28.50	69.2	70.5	69.0	4.70	4.79	4.69	2.38	2.37	2.39	4	
3/8/2015	22:10	Fine	Middle	2.5	26.33	26.33	26.33	7.66	7.66	7.66	29.97	29.97	29.98	84.8	84.5	84.4	5.76	5.75	5.74	4.73	5.03	4.83	4	4.50
	22:11		Middle	2.5	26.33	26.33	26.33	7.65	7.65	7.66	29.98	29.98	29.98	84.1	84.0	84.4	5.73	5.72	5.74	4.76	4.80	4.83	5	
5/8/2015	10:00	Fine	Middle	2.5	26.20	26.20	26.25	8.26	8.26	8.26	30.45	30.45	30.45	69.4	68.7	68.7	4.72	4.68	4.68	4.75	4.76	4.77	5	5.00
	10:02		Middle	2.5	26.30	26.30	26.25	8.26	8.26	8.26	30.44	30.44	30.45	68.5	68.0	68.7	4.66	4.64	4.68	4.79	4.79	4.77	5	
7/8/2015	11:06	Fine	Middle	2.5	27.10	27.10	27.15	8.29	8.29	8.29	30.54	30.54	30.54	72.9	72.4	72.0	4.88	4.85	4.82	6.51	6.53	6.59	10	9.50
	11:08		Middle	2.5	27.20	27.20	27.15	8.28	8.28	8.29	30.53	30.53	30.54	71.8	71.0	72.0	4.81	4.75	4.82	6.64	6.69	6.59	9	
10/8/2015	16:00	Cloudy	Middle	2.5	26.70	26.70	26.70	8.40	8.40	8.40	31.15	31.15	31.15	86.6	86.9	86.5	5.32	5.35	5.32	4.69	4.75	4.65	5	5.00
	16:02		Middle	2.5	26.70	26.70	26.70	8.39	8.39	8.40	31.15	31.15	31.15	86.3	86.3	86.5	5.30	5.30	5.32	4.58	4.57	4.65	5	
12/8/2015	17:12	Fine	Middle	2.5	27.10	27.10	27.15	8.34	8.34	8.34	31.35	31.35	31.35	75.9	75.0	73.8	5.06	5.00	4.92	4.40	4.38	4.39	8	8.00
	17:14		Middle	2.5	27.20	27.20	27.15	8.33	8.33	8.34	31.35	31.35	31.35	72.5	71.7	73.8	4.84	4.78	4.92	4.39	4.39	4.39	8	
14/8/2015	17:16	Cloudy	Middle	2.5	26.50	26.50	26.50	8.25	8.25	8.25	30.36	30.36	30.36	65.8	65.1	65.7	4.46	4.42	4.45	4.70	4.69	4.68	5	5.00
	17:18		Middle	2.5	26.50	26.50	26.50	8.25	8.25	8.25	30.36	30.36	30.36	65.3	66.5	65.7	4.42	4.51	4.45	4.65	4.66	4.68	5	
17/8/2015	9:05	Fine	Middle	3.0	25.90	25.90	19.43	8.20	8.20	8.20	30.83	30.83	30.83	72.9	73.9	74.1	4.96	5.05	5.06	4.23	4.27	4.25	6	5.00
	9:07		Middle	3.0	0.00	25.90	19.43	8.19	8.19	8.20	30.83	30.83	30.83	75.0	74.6	74.1	5.12	5.09	5.06	4.28	4.23	4.25	4	
19/8/2015	9:01	Fine	Middle	2.5	25.90	25.90	25.95	8.17	8.17	8.17	31.21	31.21	31.20	59.4	58.4	59.2	4.04	3.97	4.03	4.31	4.31	4.23	8	7.50
	9:03		Middle	2.5	26.00	26.00	25.95	8.17	8.17	8.17	31.19	31.19	31.20	59.5	59.3	59.2	4.05	4.04	4.03	4.15	4.15	4.23	7	
21/8/2015	8:58	Fine	Middle	2.5	26.10	26.10	26.15	8.18	8.18	8.18	31.29	31.29	31.29	66.9	66.0	65.7	4.54	4.47	4.45	3.27	3.32	3.35	4	3.50
	9:00		Middle	2.5	26.20	26.20	26.15	8.17	8.17	8.18	31.29	31.29	31.29	65.4	64.4	65.7	4.43	4.37	4.45	3.36	3.43	3.35	3	
25/8/2015	16:03	Fine	Middle	2.5	26.20	26.20	26.25	8.32	8.32	8.32	32.47	32.47	32.47	74.8	74.0	73.5	5.03	4.96	4.94	6.42	6.42	6.33	12	12.00
	16:05		Middle	2.5	26.30	26.30	26.25	8.31	8.31	8.32	32.47	32.47	32.47	73.6	71.5	73.5	4.95	4.80	4.94	6.19	6.27	6.33	12	
27/8/2015	16:35	Fine	Middle	2.5	26.70	26.70	26.75	8.24	8.24	8.24	32.44	32.44	32.44	74.2	73.8	74.1	4.95	4.92	4.94	6.83	6.71	6.78	8	8.00
	16:37		Middle	2.5	26.80	26.80	26.75	8.24	8.24	8.24	32.43	32.43	32.44	74.2	74.0	74.1	4.95	4.94	4.94	6.68	6.91	6.78	8	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at P1 - HKCEC Phase I  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature			pH			Salinity			DO Saturation		DO		Turbidity			Suspended Solids			
					°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	16:05	Fine	Middle	2.5	29.00	29.00	29.10	8.18	8.18	8.19	26.04	26.04	26.04	79.8	79.7	79.6	5.31	5.30	5.29	3.63	3.67	3.68	5	6.00
	16:07		Middle	2.5	29.20	29.20		8.20	8.20		26.04	26.04		79.2	79.7		5.26	5.30		3.69	3.71		7	
30/7/2015	16:45	Cloudy	Middle	2.5	27.40	27.40	27.40	8.31	8.31	8.34	26.80	26.80	26.80	87.6	86.0	86.7	5.97	5.86	5.91	6.34	6.39	6.46	10	9.50
	16:47		Middle	2.5	27.40	27.40		8.37	8.37		26.80	26.80		86.6	86.5		5.90	5.89		6.45	6.65		9	
1/8/2015	17:00	Fine	Middle	2.5	28.50	28.50	28.50	8.27	8.27	8.27	28.37	28.37	28.43	77.0	78.0	76.4	5.11	5.18	5.06	2.99	2.99	2.97	3	4.00
	17:02		Middle	2.5	28.50	28.50		8.26	8.26		28.49	28.49		75.9	74.6		5.02	4.94		2.95	2.95		5	
3/8/2015	21:50	Fine	Middle	2.5	26.27	26.27	26.27	7.64	7.64	7.64	29.53	29.53	29.53	80.0	80.2	79.6	5.47	5.49	5.45	3.56	3.48	3.48	3	3.00
	21:51		Middle	2.5	26.26	26.26		7.63	7.63		29.53	29.53		79.2	79.0		5.42	5.40		3.45	3.42		3	
5/8/2015	9:45	Fine	Middle	2.5	27.10	27.10	27.20	8.17	8.17	8.20	29.97	29.97	29.95	71.2	69.1	68.9	4.79	4.64	4.63	2.44	2.47	2.42	3	3.50
	9:47		Middle	2.5	27.30	27.30		8.22	8.22		29.92	29.92		68.0	67.3		4.57	4.53		2.47	2.31		4	
7/8/2015	10:50	Fine	Middle	2.5	29.00	29.00	29.10	8.30	8.30	8.31	29.66	29.66	29.64	86.0	83.5	84.2	5.60	5.45	5.49	3.51	3.51	3.44	5	4.50
	10:52		Middle	2.5	29.20	29.20		8.32	8.32		29.61	29.61		84.3	83.0		5.49	5.41		3.39	3.36		4	
10/8/2015	15:44	Cloudy	Middle	2.5	27.90	27.90	27.90	8.32	8.32	8.35	30.96	30.96	30.96	86.4	86.4	86.9	5.70	5.70	5.73	4.69	4.57	4.69	7	6.00
	15:46		Middle	2.5	27.90	27.90		8.37	8.37		30.95	30.95		87.3	87.4		5.76	5.77		4.68	4.81		5	
12/8/2015	16:58	Fine	Middle	2.5	27.90	27.90	28.00	8.23	8.24	8.27	31.24	31.24	31.21	75.5	72.4	72.2	4.97	4.76	4.75	4.04	4.01	3.96	8	7.50
	17:00		Middle	2.5	28.10	28.10		8.30	8.30		31.18	31.18		70.7	70.1		4.65	4.61		3.89	3.88		7	
14/8/2015	17:00	Cloudy	Middle	2.5	27.40	27.40	27.45	8.23	8.23	8.23	30.24	30.24	30.24	74.5	74.3	73.8	4.97	4.95	4.92	5.35	5.22	5.25	6	6.00
	17:02		Middle	2.5	27.50	27.50		8.23	8.23		30.23	30.23		73.7	72.7		4.92	4.85		5.14	5.28		6	
17/8/2015	8:45	Fine	Middle	3.0	27.00	27.00	27.10	8.21	8.21	8.21	31.00	31.00	31.00	78.9	79.4	79.8	5.27	5.30	5.33	4.55	4.52	4.52	3	3.00
	8:47		Middle	3.0	27.20	27.20		8.20	8.20		31.00	31.00		80.6	80.2		5.38	5.36		4.50	4.49		3	
19/8/2015	8:45	Fine	Middle	2.5	26.90	26.90	27.00	8.15	8.15	8.16	30.64	30.64	30.63	69.9	69.1	67.6	4.70	4.63	4.54	3.74	3.58	3.63	6	6.00
	8:47		Middle	2.5	27.10	27.10		8.16	8.16		30.62	30.62		66.2	65.2		4.44	4.37		3.55	3.63		6	
21/8/2015	8:42	Fine	Middle	2.5	26.90	26.90	27.00	8.15	8.15	8.17	30.84	30.84	30.82	77.8	77.3	76.3	5.22	5.18	5.12	3.75	3.75	3.76	3	3.00
	8:44		Middle	2.5	27.10	27.10		8.18	8.18		30.80	30.80		75.7	74.4		5.07	4.99		3.75	3.79		3	
25/8/2015	15:47	Fine	Middle	2.5	27.80	27.80	27.95	8.25	8.25	8.27	32.49	32.49	32.45	87.4	86.2	86.0	5.72	5.64	5.62	5.08	5.07	5.20	7	8.00
	15:49		Middle	2.5	28.10	28.10		8.29	8.29		32.41	32.41		85.5	84.7		5.58	5.53		5.21	5.44		9	
27/8/2015	16:15	Fine	Middle	2.5	27.90	27.90	28.00	8.14	8.14	8.16	32.49	32.49	32.49	82.9	83.6	83.0	5.41	5.45	5.41	4.81	4.70	4.73	2	2.50
	16:17		Middle	2.5	28.10	28.10		8.18	8.18		32.48	32.48		83.1	82.3		5.42	5.37		4.69	4.73		3	

Remarks:  
 Single underline denotes exceedance over Action Level.  
 Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at P3 - APA  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature			pH			Salinity			DO Saturation		DO		Turbidity		Suspended Solids				
					°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	16:10	Fine	Middle	2.5	28.30	28.30	28.35	8.18	8.18	8.18	26.26	26.26	26.26	77.8	78.0	78.1	5.23	5.24	5.25	2.27	2.21	2.25	3	3.50
	16:12		Middle	2.5	28.40	28.40		8.17	8.17		26.25	26.25		78.1	78.6		5.25	5.28		2.26	2.26		4	
30/7/2015	16:48	Cloudy	Middle	2.5	26.70	26.70	26.75	8.36	8.36	8.36	27.36	27.36	27.36	74.3	73.4	72.5	5.11	5.04	4.98	3.00	3.01	3.05	5	4.50
	16:50		Middle	2.5	26.80	26.80		8.35	8.35		27.35	27.35		71.7	70.7		4.93	4.85		3.08	3.11		4	
1/8/2015	17:04	Fine	Middle	2.5	27.20	27.20	27.25	8.26	8.26	13.26	28.45	28.45	28.44	74.2	73.9	72.9	5.02	5.00	4.93	1.99	2.00	2.00	3	3.00
	17:06		Middle	2.5	27.30	27.30		8.25	8.25		28.42	28.42		72.1	71.3		4.88	4.82		2.00	1.99		3	
3/8/2015	21:55	Fine	Middle	2.5	26.29	26.30	26.29	7.65	7.65	7.65	29.64	29.64	29.51	82.6	81.6	81.7	5.64	5.58	5.59	4.01	4.19	4.07	3	3.50
	21:56		Middle	2.5	26.28	26.28		7.65	7.65		29.37	29.37		81.4	81.2		5.57	5.55		4.10	3.98		4	
5/8/2015	9:48	Fine	Middle	2.5	26.60	26.60	26.65	8.22	8.22	8.22	30.37	30.37	30.35	70.5	70.4	68.9	4.77	4.76	4.66	3.02	2.98	3.00	5	4.50
	9:50		Middle	2.5	26.70	26.70		8.22	8.22		30.32	30.32		68.1	66.7		4.60	4.51		2.99	3.01		4	
7/8/2015	10:54	Fine	Middle	2.5	27.90	27.90	28.00	8.31	8.31	8.30	29.86	29.86	29.84	78.1	79.9	79.8	5.18	5.24	5.27	2.73	2.76	2.81	5	5.00
	10:56		Middle	2.5	28.10	28.10		8.29	8.29		29.82	29.82		80.1	80.9		5.30	5.36		2.81	2.94		5	
10/8/2015	15:48	Cloudy	Middle	2.5	26.90	26.90	26.95	8.37	8.37	8.38	31.16	31.16	31.16	85.0	84.4	83.6	5.69	5.65	5.60	4.61	4.60	4.46	6	5.50
	15:50		Middle	2.5	27.00	27.00		8.38	8.38		31.16	31.16		82.9	82.2		5.55	5.50		4.33	4.30		5	
12/8/2015	17:02	Fine	Middle	2.5	27.50	27.50	27.40	8.31	8.31	8.30	30.91	30.91	31.11	70.0	70.3	70.5	4.67	4.68	4.70	3.65	3.66	3.67	6	6.00
	17:04		Middle	2.5	27.30	27.30		8.28	8.28		31.31	31.31		70.7	71.1		4.71	4.73		3.68	3.70		6	
14/8/2015	17:04	Cloudy	Middle	2.5	26.60	26.60	26.65	8.23	8.23	8.23	30.33	30.33	30.33	67.4	67.6	66.9	4.56	4.57	4.53	3.64	3.72	3.69	6	5.00
	17:06		Middle	2.5	26.70	26.70		8.22	8.22		30.32	30.32		67.3	65.2		4.56	4.41		3.71	3.70		4	
17/8/2015	8:50	Fine	Middle	3.0	28.40	28.40	28.50	8.19	8.19	8.18	30.94	30.94	30.94	69.3	69.7	69.5	4.09	4.31	4.15	3.44	3.38	3.39	5	4.50
	8:52		Middle	3.0	28.60	28.60		8.17	8.17		30.94	30.94		69.0	70.0		4.07	4.14		3.37	3.37		4	
19/8/2015	8:49	Fine	Middle	2.5	26.20	26.20	26.25	8.15	8.15	8.14	30.96	30.96	30.96	61.7	60.8	60.7	4.18	4.12	4.11	3.15	3.18	3.18	5	5.50
	8:51		Middle	2.5	26.30	26.30		8.13	8.13		30.95	30.95		59.4	60.8		4.03	4.12		3.19	3.20		6	
21/8/2015	8:46	Fine	Middle	2.5	26.40	26.40	26.45	8.19	8.19	8.19	30.86	30.86	30.86	69.1	67.8	67.2	4.68	4.59	4.53	2.43	2.45	2.40	3	3.50
	8:48		Middle	2.5	26.50	26.50		8.19	8.19		30.85	30.85		66.3	65.6		4.40	4.44		2.37	2.36		4	
25/8/2015	15:51	Fine	Middle	2.5	26.90	26.90	27.00	8.29	8.29	8.28	32.55	32.55	32.52	72.1	71.4	70.8	4.79	4.74	4.70	5.57	5.95	5.63	8	8.50
	15:53		Middle	2.5	27.10	27.10		8.26	8.26		32.49	32.49		70.6	69.1		4.68	4.59		5.65	5.34		9	
27/8/2015	16:20	Fine	Middle	2.5	26.90	26.90	27.00	8.18	8.18	8.17	32.48	32.48	32.48	77.1	76.2	76.8	5.13	5.08	5.11	4.54	4.50	4.50	4	3.50
	16:22		Middle	2.5	27.10	27.10		8.16	8.16		32.47	32.47		77.4	76.5		5.14	5.09		4.49	4.45		3	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at P4 - SOC  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids						
					°C		-			ppt		%		mg/L		NTU		mg/L						
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	16:15	Fine	Middle	2.5	27.90	27.90	27.95	8.18	8.18	8.19	26.62	26.62	26.62	80.6	80.8	81.0	5.44	5.46	5.47	1.99	1.89	1.91	4	4.00
	16:17		Middle	2.5	28.00	28.00		8.19	8.19		26.62	26.62		81.3	81.1		5.49	5.47		1.88	1.88		4	
30/7/2015	16:51	Cloudy	Middle	2.5	26.80	26.80	26.80	8.36	8.36	8.36	27.59	27.59	27.59	77.5	75.0	75.1	5.21	5.14	5.12	3.58	3.63	3.68	6	6.00
	16:53		Middle	2.5	26.80	26.80		8.35	8.35		27.59	27.59		74.3	73.6		5.09	5.04		3.70	3.81		6	
1/8/2015	17:08	Fine	Middle	2.5	26.90	26.90	26.95	8.23	8.23	8.23	28.51	28.51	28.51	75.0	74.8	74.8	5.10	5.08	5.09	2.17	2.19	2.15	4	4.00
	17:10		Middle	2.5	27.00	27.00		8.22	8.22		28.51	28.51		74.9	74.6		5.09	5.07		2.19	2.04		4	
3/8/2015	21:59	Fine	Middle	2.5	26.32	26.32	26.32	7.65	7.66	7.65	29.73	29.73	29.73	89.6	89.8	89.7	6.11	6.13	6.12	4.99	5.04	5.08	3	3.50
	22:00		Middle	2.5	26.32	26.32		7.65	7.65		29.73	29.73		89.7	89.6		6.12	6.11		5.13	5.17		4	
5/8/2015	9:52	Fine	Middle	2.5	26.40	26.40	26.45	8.24	8.24	8.25	30.37	30.37	30.37	70.6	69.7	69.4	4.79	4.73	4.71	3.85	3.84	3.84	5	5.00
	9:54		Middle	2.5	26.50	26.50		8.25	8.25		30.36	30.36		68.8	68.3		4.67	4.64		3.84	3.82		5	
7/8/2015	10:58	Fine	Middle	2.5	28.10	28.10	27.85	8.28	8.28	8.28	30.21	30.21	30.22	72.5	68.2	69.5	4.83	4.54	4.63	2.86	2.53	2.62	4	4.50
	11:00		Middle	2.5	27.60	27.60		8.27	8.27		30.22	30.22		67.5	69.9		4.50	4.65		2.54	2.53		5	
10/8/2015	15:52	Cloudy	Middle	2.5	26.80	26.80	26.85	8.38	8.38	8.39	31.12	31.12	31.13	86.4	87.5	86.4	5.80	5.88	5.80	4.53	4.50	4.54	7	6.50
	15:54		Middle	2.5	26.90	26.90		8.40	8.40		31.13	31.13		87.7	84.1		5.89	5.63		4.52	4.61		6	
12/8/2015	17:05	Fine	Middle	2.5	27.20	27.20	27.25	8.29	8.29	8.30	31.54	31.54	31.54	78.6	78.0	78.0	5.23	5.19	5.19	5.65	5.57	5.54	9	9.00
	17:07		Middle	2.5	27.30	27.30		8.31	8.31		31.53	31.53		77.8	77.7		5.17	5.17		5.47	5.47		9	
14/8/2015	17:08	Cloudy	Middle	2.5	26.60	26.60	26.60	8.24	8.24	8.25	30.32	30.32	30.32	79.3	79.0	78.6	5.37	5.35	5.32	4.81	4.82	4.82	5	6.00
	17:10		Middle	2.5	26.60	26.60		8.25	8.25		30.32	30.32		78.3	77.7		5.30	5.25		4.83	4.83		7	
17/8/2015	8:55	Fine	Middle	3.0	26.40	26.40	26.45	8.19	8.19	8.19	30.83	30.83	30.83	76.2	76.6	77.1	5.16	5.18	5.15	4.33	4.30	4.30	4	4.00
	8:57		Middle	3.0	26.50	26.50		8.19	8.19		30.83	30.83		77.3	78.3		5.24	5.00		4.29	4.29		4	
19/8/2015	8:53	Fine	Middle	2.5	26.10	26.10	26.15	8.14	8.14	8.16	31.08	31.08	31.08	69.7	70.0	69.5	4.73	4.74	4.72	4.69	4.59	4.65	5	5.50
	8:55		Middle	2.5	26.20	26.20		8.17	8.17		31.07	31.07		69.2	69.2		4.70	4.70		4.65	4.67		6	
21/8/2015	8:50	Fine	Middle	2.5	26.20	26.20	26.25	8.18	8.18	8.18	31.09	31.09	31.09	70.0	70.0	69.3	4.74	4.74	4.69	3.25	3.23	3.21	4	4.00
	8:52		Middle	2.5	26.30	26.30		8.18	8.18		31.09	31.09		68.9	68.2		4.67	4.62		3.23	3.14		4	
25/8/2015	15:55	Fine	Middle	2.5	27.10	27.10	26.85	8.26	8.26	8.28	32.27	32.27	32.36	75.6	73.9	73.3	5.06	4.95	4.91	5.92	5.65	5.68	9	8.50
	15:57		Middle	2.5	26.60	26.60		8.30	8.30		32.45	32.45		71.5	72.3		4.79	4.84		5.56	5.58		8	
27/8/2015	16:25	Fine	Middle	2.5	27.00	27.00	27.05	8.19	8.19	8.20	32.43	32.43	32.44	83.4	84.2	83.7	5.54	5.59	5.55	5.03	5.05	5.04	6	6.00
	16:27		Middle	2.5	27.10	27.10		8.21	8.21		32.44	32.44		83.4	83.7		5.54	5.53		5.06	5.00		6	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at P5 - WCT / RT / IT  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids						
					°C		-		ppt		%		mg/L		NTU		mg/L							
			m	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average					
28/7/2015	16:20	Fine	Middle	2.5	27.60	27.60	27.65	8.18	8.18	8.18	26.77	26.77	26.77	78.1	75.2	75.8	5.24	5.10	5.13	1.66	1.51	1.58	3	3.50
	16:22		Middle	2.5	27.70	27.70	27.65	8.18	8.18	8.18	26.77	26.77	26.77	75.1	74.8	75.8	5.09	5.07	5.13	1.51	1.64	1.58	4	
30/7/2015	16:54	Cloudy	Middle	2.5	26.50	26.50	26.50	8.34	8.34	8.34	27.78	27.78	27.78	74.2	73.1	72.8	5.10	5.02	5.00	3.87	3.87	3.88	5	5.00
	16:56		Middle	2.5	26.50	26.50	26.50	8.34	8.34	8.34	27.77	27.77	27.77	72.2	71.6	72.8	4.95	4.93	5.00	3.82	3.96	3.88	5	
1/8/2015	17:12	Fine	Middle	2.5	26.80	26.80	26.90	8.20	8.20	8.18	28.65	28.65	28.65	67.0	70.3	68.0	4.55	4.78	4.62	2.62	2.63	2.60	4	4.00
	17:14		Middle	2.5	27.00	27.00	26.90	8.15	8.15	8.18	28.64	28.64	28.65	67.1	67.7	68.0	4.56	4.60	4.62	2.58	2.55	2.60	4	
3/8/2015	22:05	Fine	Middle	2.5	26.14	26.14	26.14	7.65	7.65	7.65	29.92	29.92	29.92	81.6	81.5	81.4	5.58	5.57	5.56	5.03	4.91	4.89	4	3.50
	22:06		Middle	2.5	26.13	26.13	26.14	7.65	7.65	7.65	29.91	29.91	29.92	81.3	81.0	81.4	5.56	5.53	5.56	4.82	4.78	4.89	3	
5/8/2015	9:56	Fine	Middle	2.5	26.30	26.30	26.35	8.26	8.26	8.26	30.39	30.39	30.39	72.3	71.7	71.6	4.91	4.87	4.87	4.80	4.68	4.71	4	4.50
	9:58		Middle	2.5	26.40	26.40	26.35	8.26	8.26	8.26	30.39	30.39	30.39	71.4	71.1	71.6	4.85	4.83	4.87	4.68	4.67	4.71	5	
7/8/2015	11:02	Fine	Middle	2.5	27.60	27.60	27.50	8.27	8.27	8.28	30.43	30.43	30.43	78.2	76.0	74.6	5.22	5.08	4.98	6.29	6.32	6.20	7	7.50
	11:04		Middle	2.5	27.40	27.40	27.50	8.29	8.29	8.28	30.42	30.42	30.43	73.1	71.1	74.6	4.88	4.75	4.98	6.20	6.00	6.20	8	
10/8/2015	15:56	Cloudy	Middle	2.5	26.70	26.70	26.75	8.40	8.40	8.40	31.15	31.15	31.15	86.1	85.5	84.8	5.79	5.77	5.70	5.39	5.55	5.52	6	6.00
	15:58		Middle	2.5	26.80	26.80	26.75	8.40	8.40	8.40	31.15	31.15	31.15	84.7	82.8	84.8	5.69	5.56	5.70	5.55	5.57	5.52	6	
12/8/2015	17:08	Fine	Middle	2.5	27.10	27.10	27.20	8.32	8.32	8.33	31.53	31.53	31.43	78.5	78.4	78.5	5.22	5.22	5.22	5.41	5.38	5.53	9	8.50
	17:10		Middle	2.5	27.30	27.30	27.20	8.33	8.33	8.33	31.33	31.33	31.43	78.6	78.3	78.5	5.23	5.21	5.22	5.62	5.71	5.53	8	
14/8/2015	17:12	Cloudy	Middle	2.5	26.50	26.40	26.48	8.25	8.25	8.26	30.36	30.36	30.36	73.3	75.2	75.0	4.97	5.10	5.09	4.74	4.71	4.74	6	5.50
	17:14		Middle	2.5	26.50	26.50	26.48	8.26	8.26	8.26	30.36	30.36	30.36	75.7	75.8	75.0	5.14	5.14	5.09	4.74	4.77	4.74	5	
17/8/2015	9:00	Fine	Middle	3.0	26.00	26.00	26.05	8.20	8.20	8.23	30.83	30.83	30.83	73.2	73.3	73.6	4.99	4.99	5.01	4.49	7.47	5.19	3	3.50
	9:02		Middle	3.0	26.10	26.10	26.05	8.30	8.20	8.23	30.83	30.83	30.83	74.2	73.5	73.6	5.06	5.00	5.01	4.41	4.40	5.19	4	
19/8/2015	8:57	Fine	Middle	2.5	25.90	25.90	26.00	8.17	8.17	8.17	31.16	31.16	31.16	69.2	68.4	68.3	4.71	4.65	4.65	4.15	4.04	4.06	7	6.50
	8:59		Middle	2.5	26.10	26.10	26.00	8.17	8.17	8.17	31.15	31.15	31.16	68.0	67.7	68.3	4.62	4.60	4.65	4.03	4.02	4.06	6	
21/8/2015	8:54	Fine	Middle	2.5	26.30	26.30	26.30	8.18	8.18	8.18	31.13	31.13	31.13	65.6	67.1	67.6	4.44	4.54	4.58	3.20	3.22	3.20	3	3.50
	8:56		Middle	2.5	26.30	26.30	26.30	8.18	8.18	8.18	31.12	31.12	31.13	68.3	69.4	67.6	4.62	4.70	4.58	3.22	3.15	3.20	4	
25/8/2015	15:59	Fine	Middle	2.5	26.30	26.30	26.35	8.31	8.31	8.32	32.26	32.26	32.28	74.8	74.2	74.0	5.02	4.98	4.97	5.76	5.76	5.76	8	8.00
	16:01		Middle	2.5	26.40	26.40	26.35	8.32	8.32	8.32	32.30	32.30	32.28	73.8	73.3	74.0	4.96	4.92	4.97	5.76	5.76	5.76	8	
27/8/2015	16:30	Fine	Middle	2.5	26.90	26.90	26.95	8.22	8.22	8.23	32.42	32.42	32.43	75.8	76.3	76.2	5.04	5.07	5.05	6.80	6.88	6.86	9	9.50
	16:32		Middle	2.5	27.00	27.00	26.95	8.23	8.23	8.23	32.43	32.43	32.43	76.4	76.1	76.2	5.08	4.99	5.05	6.88	6.89	6.86	10	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at RW21-P789 - Sun Hung Kai Centre  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids						
					°C		-		ppt		%		mg/L		NTU		mg/L							
			m	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average					
28/7/2015	16:31	Fine	Middle	3.5	27.40	27.40	27.45	8.17	8.07	8.12	26.57	26.57	26.56	65.7	66.7	66.3	4.50	4.53	4.51	2.21	2.20	2.22	5	4.00
	16:33		Middle	3.5	27.50	27.50		8.17	8.07		26.54	26.54		66.8	66.0		4.54	4.48		2.21	2.24		3	
30/7/2015	17:08	Cloudy	Middle	3.5	26.70	26.70	26.75	8.36	8.36	8.38	26.93	26.93	26.93	86.8	86.9	85.3	5.97	5.98	5.87	3.39	3.43	3.43	6	7.00
	17:10		Middle	3.5	26.80	26.80		8.40	8.40		26.93	26.93		84.3	83.0		5.80	5.71		3.44	3.46		8	
1/8/2015	21:05	Fine	Middle	3.5	25.61	25.62	25.62	7.44	7.44	7.45	29.50	29.50	29.50	80.0	80.1	80.2	5.63	5.64	5.64	2.21	2.23	2.17	4	4.00
	21:06		Middle	3.5	25.62	25.62		7.46	7.46		29.50	29.50		80.4	80.2		5.66	5.64		2.14	2.10		4	
3/8/2015	20:10	Fine	Middle	2.0	26.36	26.36	26.37	7.55	7.55	7.56	28.72	28.72	28.72	92.1	91.6	91.7	6.32	6.28	6.29	2.99	2.95	2.97	4	3.50
	20:11		Middle	2.0	26.38	26.38		7.56	7.56		28.71	28.71		91.3	91.8		6.26	6.29		3.01	2.94		3	
5/8/2015	10:08	Fine	Middle	3.5	26.00	26.00	26.10	8.25	8.25	8.26	30.04	30.04	30.02	77.2	75.4	75.6	5.28	5.15	5.17	2.56	2.53	2.53	2	2.50
	10:10		Middle	3.5	26.20	26.20		8.26	8.26		30.00	30.00		74.7	74.9		5.11	5.12		2.51	2.52		3	
7/8/2015	11:20	Fine	Middle	3.5	27.10	27.10	27.20	8.29	8.29	8.31	29.94	29.94	29.91	86.9	86.8	86.4	5.84	5.83	5.79	3.99	3.99	3.99	6	5.50
	11:22		Middle	3.5	27.30	27.30		8.32	8.32		29.88	29.88		85.9	85.9		5.76	5.73		3.99	4.00		5	
10/8/2015	16:02	Cloudy	Middle	3.0	26.40	26.40	26.45	8.40	8.40	8.40	30.91	30.91	30.91	86.1	86.4	85.9	5.32	5.34	5.29	3.87	3.91	3.93	7	6.50
	16:04		Middle	3.0	26.50	26.50		8.40	8.40		30.91	30.91		86.2	84.8		5.32	5.17		3.95	3.98		6	
12/8/2015	17:40	Fine	Middle	3.5	26.80	26.80	26.85	8.29	8.29	8.31	31.23	31.23	31.22	83.2	83.5	82.7	5.58	5.60	5.55	4.92	4.56	4.65	8	7.50
	17:42		Middle	3.5	26.90	26.90		8.33	8.33		31.20	31.20		82.8	81.4		5.55	5.46		4.56	4.55		7	
14/8/2015	21:04	Cloudy	Middle	2.5	25.40	25.40	25.40	8.23	8.23	8.23	30.44	30.44	30.44	68.2	68.6	68.2	4.74	4.74	4.72	6.02	6.01	5.99	6	6.00
	21:05		Middle	2.5	25.40	25.40		8.23	8.23		30.44	30.44		68.0	67.9		4.70	4.69		5.98	5.94		6	
17/8/2015	9:20	Fine	Middle	3.5	26.00	26.00	26.10	8.20	8.20	8.19	30.77	30.77	30.77	68.0	68.4	68.3	4.64	4.65	4.65	3.56	3.53	3.56	4	4.00
	9:22		Middle	3.5	26.20	26.20		8.18	8.18		30.77	30.77		67.9	68.8		4.62	4.68		3.52	3.63		4	
19/8/2015	9:10	Fine	Middle	3.5	26.10	26.10	26.15	8.17	8.17	8.17	30.71	30.71	30.70	72.6	70.3	69.4	4.94	4.79	4.72	3.75	3.75	3.76	7	7.50
	9:12		Middle	3.5	26.20	26.20		8.17	8.17		30.68	30.68		68.1	66.6		4.63	4.53		3.75	3.77		8	
21/8/2015	9:05	Fine	Middle	3.5	26.20	26.20	26.25	8.18	8.18	8.19	31.05	31.05	31.05	72.3	71.9	71.1	4.90	4.87	4.82	3.81	3.81	3.82	3	3.00
	9:07		Middle	3.5	26.30	26.30		8.19	8.19		31.04	31.04		70.6	69.5		4.79	4.71		3.82	3.83		3	
25/8/2015	16:13	Fine	Middle	3.5	26.70	26.70	26.80	8.28	8.28	8.29	32.20	32.20	32.22	77.7	76.1	76.2	5.18	5.07	5.07	4.56	4.62	4.63	9	9.50
	16:15		Middle	3.5	26.90	26.90		8.30	8.30		32.24	32.24		75.8	75.0		5.05	4.99		4.66	4.67		10	
27/8/2015	16:50	Fine	Middle	3.5	26.70	26.70	26.80	8.24	8.24	8.25	32.42	32.42	32.42	79.0	79.4	78.8	5.27	5.29	5.25	8.55	8.45	8.47	12	12.50
	16:52		Middle	3.5	26.90	26.90		8.25	8.25		32.42	32.42		78.5	78.4		5.23	5.22		8.44	8.44		13	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at WSD19 - Sheung Wan  
Mid-Flood Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature			pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids					
					°C		-		ppt		%		mg/L		NTU		mg/L							
			m	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average					
28/7/2015	15:21	Fine	Middle	3.5	28.70	28.70	28.40	8.27	8.27	8.25	26.30	26.30	26.26	76.3	75.1	74.5	5.09	5.01	4.97	2.55	2.53	2.53	5	5.00
	15:23		Middle	3.5	28.10	28.10		8.23	8.23		26.22	26.22		73.7	73.0		4.91	4.86		2.52	2.52		5	
30/7/2015	16:04	Cloudy	Middle	3.5	27.00	27.00	27.10	8.34	8.34	8.34	27.58	27.58	27.57	74.2	73.1	71.9	5.06	4.95	4.89	3.88	3.22	3.58	8	8.50
	16:06		Middle	3.5	27.20	27.20		8.33	8.33		27.55	27.55		70.7	69.4		4.81	4.72		3.35	3.86		9	
1/8/2015	18:52	Fine	Middle	3.0	26.22	26.22	26.22	7.73	7.73	7.72	29.00	29.00	29.01	96.4	96.1	96.1	6.73	6.70	6.71	2.61	2.70	2.58	5	4.50
	18:53		Middle	3.0	26.22	26.22		7.70	7.73		29.01	29.01		96.5	95.4		6.73	6.66		2.57	2.45		4	
3/8/2015	20:50	Fine	Middle	2.5	26.04	26.04	26.06	7.28	7.29	7.30	29.40	29.40	29.40	98.7	98.7	98.6	6.77	6.77	6.77	4.36	4.83	4.40	2	2.00
	20:51		Middle	2.5	26.08	26.08		7.31	7.31		29.39	29.39		98.6	98.4		6.77	6.75		4.26	4.14		2	
5/8/2015	8:40	Fine	Middle	3.5	26.50	26.50	26.55	8.23	8.23	8.23	29.33	29.33	29.33	65.0	65.0	63.5	4.44	4.45	4.33	3.53	3.52	3.52	4	4.00
	8:42		Middle	3.5	26.60	26.60		8.22	8.22		29.33	29.33		62.4	61.4		4.25	4.18		3.52	3.51		4	
7/8/2015	9:54	Fine	Middle	3.5	28.60	28.60	28.70	8.37	8.37	8.37	29.30	29.30	29.28	81.7	82.1	80.8	5.37	5.40	5.31	3.64	3.69	3.70	9	9.00
	9:56		Middle	3.5	28.80	28.80		8.36	8.36		29.26	29.26		80.3	79.1		5.27	5.20		3.72	3.73		9	
10/8/2015	14:40	Cloudy	Middle	3.0	26.90	26.90	27.00	8.36	8.36	8.40	30.70	30.70	30.70	98.6	98.7	98.8	6.62	6.62	6.62	5.95	5.77	5.81	9	8.00
	14:42		Middle	3.0	27.10	27.10		8.44	8.44		30.70	30.70		99.7	98.0		6.68	6.57		5.76	5.76		7	
12/8/2015	16:10	Fine	Middle	3.5	28.60	28.60	28.50	8.29	8.29	8.31	30.72	30.72	30.72	83.2	81.4	80.8	5.45	5.32	5.29	5.19	5.21	5.12	7	7.00
	16:12		Middle	3.5	28.40	28.40		8.32	8.32		30.71	30.71		79.7	79.0		5.21	5.17		5.14	4.95		7	
14/8/2015	20:10	Cloudy	Middle	2.5	25.40	25.40	25.40	8.12	8.12	8.13	30.49	30.49	30.50	75.0	74.8	73.6	5.17	5.16	5.07	4.24	4.22	4.20	5	5.00
	20:11		Middle	2.5	25.40	25.40		8.14	8.14		30.50	30.50		71.8	72.8		4.91	5.02		4.20	4.14		5	
17/8/2015	7:05	Fine	Middle	3.5	25.60	25.60	25.70	8.20	8.20	8.19	31.29	31.29	31.29	62.2	61.0	60.4	4.15	4.16	4.10	8.32	8.28	8.31	8	8.00
	7:07		Middle	3.5	25.80	25.80		8.17	8.17		31.29	31.29		58.9	59.5		4.02	4.06		8.29	8.36		8	
19/8/2015	8:18	Fine	Middle	3.5	26.90	26.90	26.95	8.24	8.24	8.23	29.77	29.77	29.78	61.5	62.1	61.3	4.15	4.19	4.13	3.87	3.87	3.87	5	5.00
	8:20		Middle	3.5	27.00	27.00		8.21	8.21		29.78	29.78		61.4	60.0		4.14	4.03		3.87	3.88		5	
21/8/2015	7:53	Fine	Middle	3.5	26.60	26.60	26.65	8.26	8.26	8.26	30.27	30.27	30.27	60.0	59.6	59.3	4.06	4.03	4.01	7.03	6.97	7.04	3	3.00
	7:55		Middle	3.5	26.70	26.70		8.25	8.25		30.26	30.26		59.0	58.5		3.99	3.95		7.00	7.16		3	
25/8/2015	15:05	Fine	Middle	3.5	27.70	27.70	27.80	8.39	8.39	8.38	32.51	32.51	32.52	70.7	70.0	71.0	4.63	4.57	4.64	7.76	7.63	7.61	12	12.50
	15:07		Middle	3.5	27.90	27.90		8.37	8.37		32.53	32.53		70.7	72.6		4.62	4.75		7.51	7.53		13	
27/8/2015	15:21	Fine	Middle	3.5	27.00	27.00	27.15	8.27	8.27	8.27	32.62	32.62	32.58	64.1	64.2	63.7	4.24	4.25	4.21	8.72	8.89	8.88	8	8.00
	15:23		Middle	3.5	27.30	27.30		8.26	8.26		32.54	32.54		63.6	62.8		4.21	4.15		8.99	8.91		8	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at C7 - Windsor House  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH		Salinity		DO Saturation		DO		Turbidity		Suspended Solids							
					°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average						
28/7/2015	-	Fine	Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-					
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-					
30/7/2015	11:43	Fine	Middle	-	27.50	27.50	27.55	8.19	8.19	8.19	28.07	28.07	28.07	69.7	72.5	71.9	4.70	4.89	4.85	1.88	1.84	1.85	4	3.50
	11:45		Middle	-	27.60	27.60	27.55	8.19	8.19	8.19	28.07	28.07	28.07	72.6	72.9	71.9	4.89	4.92	4.85	1.82	1.85	1.85	3	3.50
1/8/2015	15:05	Fine	Middle	-	28.20	28.20	28.45	8.23	8.23	8.19	29.52	29.52	29.50	72.6	71.7	71.7	4.79	4.73	4.73	1.64	1.64	1.58	3	3.50
	15:07		Middle	-	28.70	28.70	28.45	8.15	8.15	8.19	29.48	29.48	29.50	71.0	71.4	71.7	4.68	4.70	4.73	1.53	1.52	1.58	4	3.50
3/8/2015	15:20	Fine	Middle	-	27.60	27.60	27.80	8.12	8.12	8.13	20.46	20.46	18.90	76.9	77.0	76.3	5.55	5.52	5.45	1.84	1.80	1.80	3	3.00
	15:22		Middle	-	28.00	28.00	27.80	8.13	8.13	8.13	16.64	18.02	18.90	75.0	76.2	76.3	5.36	5.37	5.45	1.79	1.78	1.80	3	3.00
5/8/2015	16:15	Fine	Middle	-	27.90	27.90	28.10	8.23	8.23	8.22	29.93	29.93	29.93	74.6	73.8	74.3	4.93	4.88	4.91	2.30	2.29	2.29	4	3.50
	16:17		Middle	-	28.30	28.30	28.10	8.20	8.20	8.22	29.92	29.92	29.93	74.0	74.8	74.3	4.89	4.94	4.91	2.28	2.27	2.29	3	3.50
7/8/2015	18:20	Sunny	Middle	-	28.10	28.10	28.15	8.25	8.25	8.24	29.99	29.99	29.98	69.2	69.4	68.8	4.57	4.59	4.55	2.75	2.73	2.66	7	7.00
	18:22		Middle	-	28.20	28.20	28.15	8.23	8.23	8.24	29.96	29.96	29.98	68.7	68.0	68.8	4.54	4.49	4.55	2.59	2.58	2.66	7	7.00
10/8/2015	10:25	Cloudy	Middle	-	27.10	27.10	27.10	8.27	8.27	8.28	30.25	30.25	30.27	80.9	81.8	81.2	5.43	5.47	5.45	2.20	2.25	2.24	7	7.50
	10:27		Middle	-	27.10	27.10	27.10	8.28	8.28	8.28	30.28	30.28	30.27	80.9	81.2	81.2	5.43	5.45	5.45	2.26	2.26	2.24	8	7.50
12/8/2015	11:45	Sunny	Middle	-	27.40	27.40	27.45	8.17	8.17	8.17	31.15	31.15	31.15	65.8	68.4	68.1	4.44	4.54	4.54	8.15	8.07	8.04	4	4.50
	11:47		Middle	-	27.50	27.50	27.45	8.16	8.16	8.17	31.15	31.15	31.15	68.9	69.2	68.1	4.57	4.59	4.54	8.00	7.92	8.04	5	4.50
14/8/2015	13:58	Cloudy	Middle	-	26.70	26.70	26.75	8.17	8.17	8.16	30.11	30.11	30.10	68.6	68.8	67.6	4.61	4.65	4.56	2.51	2.51	2.49	6	5.50
	14:00		Middle	-	26.80	26.80	26.75	8.15	8.15	8.16	30.09	30.09	30.10	67.8	65.2	67.6	4.58	4.40	4.56	2.56	2.37	2.49	5	5.50
17/8/2015	11:35	Fine	Middle	-	26.50	26.50	26.70	8.13	8.13	8.13	30.38	30.38	30.38	68.0	68.1	67.9	4.59	4.59	4.58	2.76	2.75	2.77	4	4.00
	11:37		Middle	-	26.90	26.90	26.70	8.12	8.12	8.13	30.38	30.38	30.38	68.0	67.5	67.9	4.58	4.55	4.58	2.77	2.78	2.77	4	4.00
19/8/2015	15:30	Sunny	Middle	-	28.20	28.20	28.30	8.05	8.05	8.06	30.45	30.45	30.45	58.2	58.2	58.7	3.83	3.82	3.86	3.71	3.72	3.70	4	4.00
	15:32		Middle	-	28.40	28.40	28.30	8.06	8.06	8.06	30.44	30.44	30.45	58.7	59.5	58.7	3.86	3.91	3.86	3.65	3.70	3.70	4	4.00
21/8/2015	15:00	Fine	Middle	-	27.80	27.80	27.65	8.11	8.11	8.12	31.47	31.47	31.47	65.5	64.8	63.6	4.35	4.30	4.22	2.73	2.74	2.73	3	3.00
	15:02		Middle	-	27.50	27.50	27.65	8.12	8.12	8.12	31.47	31.47	31.47	63.4	60.8	63.6	4.21	4.03	4.22	2.65	2.79	2.73	3	3.00
25/8/2015	10:00	Fine	Middle	-	27.00	27.00	27.10	8.18	8.18	8.17	32.17	32.17	32.17	75.6	74.8	74.6	5.03	4.97	4.95	2.47	2.46	2.46	7	7.00
	10:02		Middle	-	27.20	27.20	27.10	8.16	8.16	8.17	32.17	32.17	32.17	74.9	72.9	74.6	4.97	4.84	4.95	2.45	2.47	2.46	7	7.00
27/8/2015	11:09	Fine	Middle	-	27.40	27.40	27.50	8.11	8.11	8.11	32.40	32.40	32.40	64.8	64.3	63.6	4.27	4.23	4.19	1.98	1.98	1.98	2	2.50
	11:11		Middle	-	27.60	27.60	27.50	8.11	8.11	8.11	32.39	32.39	32.40	63.5	61.9	63.6	4.18	4.07	4.19	1.98	1.98	1.98	3	2.50

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at C1 - HKCEC  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature			pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids					
					°C			-			ppt		%		mg/L		NTU		mg/L					
					Value	Average		Value	Average		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	11:40	Fine	Middle	2.5	27.60	27.60	27.65	8.23	8.23	8.23	24.63	24.63	24.48	83.7	83.8	83.9	5.75	5.76	5.76	2.27	2.27	2.27	5	5.00
	11:42		Middle	2.5	27.70	27.70		8.23	8.23		24.32	24.32		84.0	84.0		5.77	5.77		2.26	2.26		5	
30/7/2015	11:00	Fine	Middle	2.5	27.50	27.50	27.55	8.38	8.38	8.38	26.95	26.95	26.95	79.0	80.1	79.5	5.37	5.44	5.40	3.00	3.00	2.99	4	3.50
	11:02		Middle	2.5	27.60	27.60		8.38	8.38		26.94	26.94		79.8	79.0		5.42	5.36		2.97	2.97		3	
1/8/2015	11:00	Fine	Middle	2.5	26.50	26.50	26.55	8.22	8.22	8.22	29.26	29.26	29.26	67.9	69.5	68.7	4.63	4.74	4.69	2.23	2.21	2.21	3	3.50
	11:02		Middle	2.5	26.60	26.60		8.22	8.22		29.26	29.26		69.1	68.4		4.71	4.66		2.20	2.20		4	
3/8/2015	14:30	Fine	Middle	2.5	26.80	26.80	26.80	8.30	8.30	8.30	29.19	29.19	29.20	71.4	71.6	71.8	4.85	4.86	4.87	2.52	2.44	2.47	2	2.00
	14:32		Middle	2.5	26.80	26.80		8.30	8.30		29.20	29.20		71.7	72.3		4.87	4.91		2.45	2.46		2	
5/8/2015	15:14	Fine	Middle	2.5	26.90	26.90	26.95	8.37	8.37	8.37	29.85	29.85	29.85	84.1	81.5	80.0	5.67	5.49	5.42	2.68	2.70	2.66	6	5.00
	15:16		Middle	2.5	27.00	27.00		8.37	8.37		29.85	29.85		76.4	77.9		5.28	5.25		2.70	2.54		4	
7/8/2015	16:58	Sunny	Middle	2.5	28.10	28.10	28.10	8.50	8.50	8.49	30.49	30.49	30.49	97.0	96.7	96.6	6.40	6.38	6.37	3.97	3.87	3.84	4	4.00
	17:00		Middle	2.5	28.10	28.10		8.48	8.48		30.49	30.49		96.0	96.6		6.33	6.37		3.76	3.74		4	
10/8/2015	9:50	Cloudy	Middle	3.0	26.70	26.70	26.70	8.48	8.48	8.48	30.40	30.40	30.40	93.4	93.8	93.2	6.31	6.32	6.29	2.96	2.98	3.00	3	3.50
	9:52		Middle	3.0	26.70	26.70		8.48	8.48		30.40	30.40		92.9	92.7		6.27	6.26		2.99	3.08		4	
12/8/2015	10:54	Sunny	Middle	2.5	26.80	26.80	26.80	8.37	8.37	8.37	30.78	30.78	30.79	76.0	76.1	77.1	5.12	5.12	5.19	3.22	3.23	3.22	6	6.00
	10:56		Middle	2.5	26.80	26.80		8.37	8.37		30.79	30.79		77.1	79.0		5.19	5.32		3.22	3.19		6	
14/8/2015	11:16	Cloudy	Middle	2.5	26.40	26.40	26.40	8.30	8.30	8.30	30.02	30.02	30.02	72.5	73.3	72.3	4.93	4.99	4.92	3.20	3.24	3.08	4	3.50
	11:18		Middle	2.5	26.40	26.40		8.30	8.30		30.02	30.02		72.3	71.2		4.91	4.84		3.00	2.88		3	
17/8/2015	15:35	Fine	Middle	2.5	27.00	27.00	27.10	8.19	8.19	8.19	30.55	30.55	30.55	76.8	77.9	77.8	5.15	5.22	5.22	4.58	4.67	4.66	4	4.00
	15:37		Middle	2.5	27.20	27.20		8.19	8.19		30.55	30.55		78.2	78.4		5.24	5.25		4.70	4.69		4	
19/8/2015	14:25	Sunny	Middle	2.5	27.20	27.20	27.25	8.20	8.20	8.20	30.47	30.47	30.48	77.9	78.0	77.8	5.21	5.22	5.21	2.86	2.79	2.85	5	5.00
	14:27		Middle	2.5	27.30	27.30		8.20	8.20		30.48	30.48		77.2	78.2		5.16	5.25		2.82	2.92		5	
21/8/2015	16:37	Fine	Middle	2.5	26.70	26.70	26.70	8.29	8.29	8.29	31.44	31.44	31.44	72.1	73.0	73.2	4.85	4.91	4.92	3.32	3.27	3.27	3	3.00
	16:39		Middle	2.5	26.70	26.70		8.29	8.29		31.44	31.44		73.6	73.9		4.94	4.97		3.26	3.23		3	
25/8/2015	9:15	Fine	Middle	2.5	25.90	25.90	25.95	8.38	8.38	8.38	32.20	32.20	32.19	77.9	77.1	77.3	5.28	5.22	5.24	4.28	4.28	4.43	6	5.00
	9:17		Middle	2.5	26.00	26.00		8.37	8.37		32.18	32.18		76.6	77.7		5.19	5.26		4.48	4.68		4	
27/8/2015	9:16	Fine	Middle	2.5	26.10	26.10	26.10	8.29	8.29	8.29	32.77	32.77	32.77	66.6	65.2	64.9	4.49	4.39	4.37	6.00	5.95	5.95	8	7.50
	9:18		Middle	2.5	26.10	26.10		8.29	8.29		32.76	32.76		64.3	63.5		4.33	4.26		5.75	6.11		7	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at P1 - HKCEC Phase I  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature			pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids					
					°C			-			ppt		%		mg/L		NTU		mg/L					
					Value	Average		Value	Average		Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	11:20	Fine	Middle	2.5	28.50	28.50	28.50	8.19	8.19	8.20	24.72	24.72	24.72	91.5	90.1	89.8	6.20	6.11	6.09	1.49	1.34	1.41	4	3.00
	11:22		Middle	2.5	28.50	28.50		8.21	8.21		24.72	24.72		89.5	88.2		6.06	5.97		1.36	1.45		2	
30/7/2015	10:45	Fine	Middle	2.5	28.00	28.00	28.05	8.20	8.20	8.27	26.37	26.37	26.35	83.3	81.4	80.2	5.62	5.48	5.41	2.30	2.32	2.33	4	4.00
	10:47		Middle	2.5	28.10	28.10		8.34	8.34		26.33	26.32		79.1	77.0		5.33	5.19		2.34	2.35		4	
1/8/2015	10:45	Fine	Middle	2.5	27.20	27.20	27.25	8.19	8.19	8.20	29.27	29.27	29.26	72.7	70.6	70.4	4.90	4.75	4.74	1.81	1.81	1.85	3	3.50
	10:47		Middle	2.5	27.30	27.30		8.21	8.21		29.25	29.25		69.1	69.1		4.66	4.65		1.86	1.92		4	
3/8/2015	14:13	Fine	Middle	2.5	27.60	27.60	27.85	8.14	8.14	8.18	29.74	29.74	29.70	73.7	74.7	74.2	4.92	4.98	4.95	2.37	2.37	2.34	3	3.50
	14:15		Middle	2.5	28.10	28.10		8.21	8.21		29.65	29.65		75.0	73.2		5.00	4.88		2.29	2.31		4	
5/8/2015	15:00	Fine	Middle	2.5	27.50	27.50	27.55	8.28	8.28	8.30	29.99	29.99	29.97	74.0	72.8	72.3	4.93	4.86	4.83	2.78	2.76	2.76	4	3.50
	15:02		Middle	2.5	27.60	27.60		8.32	8.32		29.94	29.94		71.8	70.7		4.79	4.72		2.75	2.75		3	
7/8/2015	16:42	Sunny	Middle	2.5	28.60	28.60	28.60	8.39	8.39	8.44	30.10	30.10	30.15	103.5	105.6	104.2	6.72	6.87	6.78	5.22	5.10	5.13	6	6.00
	16:44		Middle	2.5	28.60	28.60		8.48	8.48		30.20	30.20		103.9	103.9		6.76	6.76		5.19	5.00		6	
10/8/2015	9:30	Cloudy	Middle	3.0	27.00	27.00	27.10	8.39	8.39	8.42	30.14	30.14	30.29	99.3	98.7	98.2	6.66	6.61	6.58	3.73	3.73	3.72	5	5.00
	9:32		Middle	3.0	27.20	27.20		8.45	8.45		30.43	30.43		97.1	97.5		6.50	6.53		3.71	3.71		5	
12/8/2015	10:38	Sunny	Middle	2.5	27.50	27.50	27.65	8.29	8.29	8.32	30.73	30.73	30.71	82.2	81.3	81.2	5.46	5.39	5.39	3.39	3.38	3.42	5	5.00
	10:40		Middle	2.5	27.80	27.80		8.34	8.34		30.69	30.69		80.4	80.7		5.34	5.35		3.43	3.48		5	
14/8/2015	11:00	Cloudy	Middle	2.5	26.40	26.40	26.45	8.25	8.25	8.27	30.31	30.31	30.16	71.8	72.6	71.8	4.88	4.94	4.88	3.00	2.99	2.98	7	6.00
	11:02		Middle	2.5	26.50	26.50		8.28	8.28		30.00	30.00		71.8	70.8		4.88	4.81		2.97	2.97		5	
17/8/2015	15:15	Fine	Middle	2.5	29.80	29.80	29.80	8.16	8.16	8.18	30.57	30.57	30.61	87.4	86.3	86.3	5.71	5.62	5.62	4.50	4.67	4.63	5	5.00
	15:17		Middle	2.5	29.80	29.80		8.19	8.19		30.65	30.65		85.7	85.7		5.58	5.58		4.68	4.68		5	
19/8/2015	14:05	Sunny	Middle	2.5	28.80	28.80	28.85	8.08	8.08	8.11	30.75	30.75	30.74	90.4	91.2	89.9	5.89	5.93	5.86	2.70	2.72	2.72	5	4.50
	14:07		Middle	2.5	28.90	28.90		8.13	8.13		30.73	30.73		89.5	88.6		5.82	5.78		2.73	2.74		4	
21/8/2015	16:21	Fine	Middle	2.5	27.70	27.70	27.75	8.19	8.19	8.21	31.48	31.48	31.45	76.4	73.5	73.1	5.04	4.85	4.82	3.27	3.34	3.28	3	3.00
	16:23		Middle	2.5	27.80	27.80		8.23	8.23		31.42	31.42		71.6	70.7		4.73	4.66		3.26	3.25		3	
25/8/2015	8:59	Fine	Middle	2.5	26.40	26.40	26.65	8.19	8.19	8.24	31.89	31.89	31.73	81.8	81.3	80.9	5.49	5.45	5.42	3.63	3.62	3.62	6	6.50
	9:01		Middle	2.5	26.90	26.90		8.29	8.29		31.56	31.56		80.7	79.7		5.40	5.34		3.61	3.60		7	
27/8/2015	9:00	Fine	Middle	2.5	26.60	26.60	26.70	8.24	8.24	8.25	32.81	32.82	32.81	74.8	74.3	74.1	4.99	4.95	4.94	3.87	3.87	3.89	5	4.50
	9:02		Middle	2.5	26.80	26.80		8.26	8.26		32.81	32.81		73.7	73.5		4.91	4.90		3.90	3.93		4	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at P3 - APA  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature			pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids					
					°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	11:25	Fine	Middle	2.5	28.40	28.40	28.20	8.22	8.22	8.22	23.32	23.32	23.66	86.7	85.3	85.7	5.92	5.84	5.86	1.14	1.03	1.09	4	4.50
	11:27		Middle	2.5	28.00	28.00		8.22	8.22		24.00	24.00		85.7	85.2		5.86	5.83		1.13	1.07		5	
30/7/2015	10:49	Fine	Middle	2.5	27.80	27.80	27.80	8.36	8.36	8.37	26.76	26.76	26.76	84.4	85.1	83.9	5.72	5.77	5.68	2.75	2.75	2.75	4	4.00
	10:51		Middle	2.5	27.80	27.80		8.37	8.37		26.76	26.76		83.3	82.7		5.64	5.60		2.75	2.75		4	
1/8/2015	10:49	Fine	Middle	2.5	26.80	26.80	26.90	8.22	8.22	8.22	29.10	29.10	29.09	68.0	69.5	69.9	4.61	4.71	4.74	2.02	2.01	1.95	2	3.00
	10:51		Middle	2.5	27.00	27.00		8.22	8.22		29.07	29.07		70.8	71.4		4.80	4.84		1.88	1.87		4	
3/8/2015	14:17	Fine	Middle	2.5	27.20	27.20	27.30	8.24	8.24	8.26	29.34	29.33	29.31	76.4	75.2	76.6	5.14	5.05	5.17	2.27	2.37	2.38	2	2.00
	14:19		Middle	2.5	27.40	27.40		8.27	8.27		29.28	29.28		78.0	76.9		5.30	5.17		2.51	2.38		2	
5/8/2015	15:03	Fine	Middle	2.5	27.10	27.10	27.15	8.34	8.34	8.35	29.87	29.87	29.86	74.4	74.0	73.9	5.00	4.98	4.97	2.31	2.32	2.30	4	4.50
	15:05		Middle	2.5	27.20	27.20		8.36	8.36		29.85	29.85		73.6	73.5		4.95	4.94		2.29	2.28		5	
7/8/2015	16:46	Sunny	Middle	2.5	27.90	27.90	27.95	8.52	8.52	8.53	30.22	30.22	30.22	100.8	101.2	102.2	6.66	6.70	6.77	3.86	3.87	3.91	6	6.50
	16:48		Middle	2.5	28.00	28.00		8.54	8.54		30.21	30.21		103.0	103.9		6.82	6.88		4.00	3.90		7	
10/8/2015	9:35	Cloudy	Middle	3.0	26.70	26.70	26.70	8.47	8.47	8.48	30.40	30.40	30.40	95.7	97.5	96.1	6.46	6.58	6.49	3.68	3.69	3.67	5	4.50
	9:37		Middle	3.0	26.70	26.70		8.48	8.48		30.40	30.40		96.2	95.0		6.50	6.41		3.64	3.65		4	
12/8/2015	10:42	Sunny	Middle	2.5	26.80	26.80	26.90	8.36	8.36	8.37	30.74	30.74	30.71	83.5	82.1	82.3	5.61	5.52	5.53	3.64	3.79	3.72	4	5.00
	10:44		Middle	2.5	27.00	27.00		8.37	8.37		30.67	30.67		81.7	81.9		5.49	5.50		3.80	3.65		6	
14/8/2015	11:04	Cloudy	Middle	2.5	26.20	26.20	26.25	8.29	8.29	8.30	30.00	30.00	30.00	74.6	74.2	73.4	5.09	5.06	5.01	2.74	2.74	2.69	5	5.00
	11:06		Middle	2.5	26.30	26.30		8.30	8.30		30.00	30.00		73.0	71.8		4.98	4.90		2.64	2.64		5	
17/8/2015	15:20	Fine	Middle	2.5	27.40	27.40	27.55	8.19	8.19	8.20	30.59	30.59	30.59	81.2	80.9	82.1	5.20	5.18	5.26	5.09	5.28	5.23	4	3.50
	15:22		Middle	2.5	27.70	27.70		8.20	8.20		30.58	30.58		82.9	83.2		5.31	5.34		5.28	5.25		3	
19/8/2015	14:10	Sunny	Middle	2.5	27.90	27.90	28.00	8.16	8.16	8.17	30.39	30.39	30.42	83.8	84.2	84.0	5.54	5.57	5.56	2.37	2.31	2.31	4	4.00
	14:12		Middle	2.5	28.10	28.10		8.18	8.18		30.44	30.44		83.9	84.2		5.54	5.58		2.29	2.28		4	
21/8/2015	16:25	Fine	Middle	2.5	27.00	27.00	27.05	8.26	8.26	8.27	31.37	31.37	31.37	69.6	69.2	69.1	4.65	4.62	4.61	3.25	3.25	3.25	3	2.50
	16:27		Middle	2.5	27.10	27.10		8.27	8.27		31.37	31.37		68.9	68.6		4.60	4.58		3.25	3.26		2	
25/8/2015	9:03	Fine	Middle	2.5	26.20	26.20	26.25	8.33	8.33	8.34	32.17	32.17	32.16	83.3	81.2	81.5	5.61	5.47	5.49	3.61	3.62	3.59	5	6.00
	9:05		Middle	2.5	26.30	26.30		8.35	8.35		32.14	32.14		81.3	80.0		5.47	5.39		3.58	3.54		7	
27/8/2015	9:04	Fine	Middle	2.5	26.10	26.10	26.15	8.27	8.27	8.28	32.80	32.80	32.78	64.7	64.8	65.0	4.36	4.36	4.38	4.21	4.21	4.21	5	5.00
	9:06		Middle	2.5	26.20	26.20		8.28	8.28		32.76	32.76		65.3	65.2		4.40	4.39		4.21	4.21		5	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at P4 - SOC  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids						
					°C		-			ppt		%		mg/L		NTU		mg/L						
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	11:30	Fine	Middle	2.5	27.80	27.80	27.85	8.23	8.23	8.23	24.12	24.12	24.12	87.0	86.4	86.5	5.93	5.90	5.91	0.99	0.99	0.99	5	5.50
	11:32		Middle	2.5	27.90	27.90		8.23	8.23		24.12	24.12		86.5	86.1		5.91	5.89		1.00	0.97		6	
30/7/2015	10:53	Fine	Middle	2.5	27.50	27.50	27.50	8.38	8.38	8.39	26.76	26.76	26.76	79.0	79.4	78.9	5.38	5.41	5.37	2.07	2.03	2.03	2	2.50
	10:55		Middle	2.5	27.50	27.50		8.39	8.39		26.75	26.75		79.1	78.2		5.38	5.32		2.01	2.00		3	
1/8/2015	10:52	Fine	Middle	2.5	26.50	26.50	26.60	8.22	8.22	8.22	25.37	25.37	25.08	73.2	74.5	74.1	5.09	5.18	5.16	1.79	1.78	1.79	3	3.00
	10:54		Middle	2.5	26.70	26.70		8.22	8.22		24.78	24.78		74.4	74.4		5.18	5.17		1.79	1.80		3	
3/8/2015	14:22	Fine	Middle	2.5	26.80	26.80	26.85	8.28	8.28	8.29	29.32	29.32	29.32	73.2	75.7	74.4	4.96	5.13	5.03	2.64	3.00	2.77	4	4.50
	14:24		Middle	2.5	26.90	26.90		8.29	8.29		29.31	29.31		75.0	73.5		5.03	4.98		2.74	2.68		5	
5/8/2015	15:06	Fine	Middle	2.5	27.10	27.10	27.10	8.37	8.37	8.37	29.33	29.33	29.33	76.3	79.1	79.3	5.14	5.32	5.34	2.19	2.21	2.21	5	4.50
	15:08		Middle	2.5	27.10	27.10		8.37	8.37		29.33	29.33		81.1	80.5		5.46	5.42		2.21	2.21		4	
7/8/2015	16:50	Sunny	Middle	2.5	28.00	28.00	28.05	8.52	8.52	8.52	30.33	30.33	30.33	99.0	98.3	97.7	6.54	6.49	6.45	4.28	4.22	4.21	6	6.50
	16:52		Middle	2.5	28.10	28.10		8.51	8.51		30.32	30.32		97.4	96.1		6.43	6.34		4.10	4.22		7	
10/8/2015	9:40	Cloudy	Middle	3.0	26.70	26.70	26.75	8.48	8.48	8.48	30.37	30.37	30.38	96.0	96.1	95.9	6.48	6.49	6.47	3.55	3.54	3.53	4	3.50
	9:42		Middle	3.0	26.80	26.80		8.48	8.48		30.39	30.39		96.3	95.0		6.50	6.41		3.52	3.52		3	
12/8/2015	10:46	Sunny	Middle	2.5	27.00	27.00	27.05	8.37	8.37	8.37	30.70	30.70	30.70	78.7	78.0	77.2	5.27	5.23	5.17	3.74	3.73	3.73	6	5.50
	10:48		Middle	2.5	27.10	27.10		8.36	8.36		30.70	30.70		76.9	75.0		5.15	5.03		3.72	3.73		5	
14/8/2015	11:08	Cloudy	Middle	2.5	26.20	26.20	26.20	8.30	8.30	8.30	30.00	30.00	30.00	78.8	77.9	76.4	5.38	5.32	5.22	3.52	3.52	3.43	4	4.00
	11:10		Middle	2.5	26.20	26.20		8.30	8.30		30.00	30.00		74.9	74.0		5.11	5.05		3.36	3.32		4	
17/8/2015	15:25	Fine	Middle	2.5	27.50	27.50	27.60	8.19	8.19	8.19	30.54	30.54	30.55	84.6	84.0	84.3	5.43	5.40	5.42	4.29	4.29	4.27	4	4.50
	15:27		Middle	2.5	27.70	27.70		8.19	8.19		30.56	30.56		84.2	84.5		5.42	5.44		4.26	4.23		5	
19/8/2015	14:15	Sunny	Middle	2.5	27.80	27.80	27.90	8.19	8.19	8.20	30.38	30.38	30.39	84.9	84.7	84.8	5.62	5.61	5.62	2.74	2.74	2.74	4	5.00
	14:17		Middle	2.5	28.00	28.00		8.20	8.20		30.39	30.39		84.9	84.7		5.62	5.61		2.74	2.75		6	
21/8/2015	16:29	Fine	Middle	2.5	26.80	26.80	26.85	8.27	8.27	8.27	31.38	31.38	31.38	73.8	73.3	73.6	4.94	4.91	4.93	2.25	2.27	2.21	3	3.00
	16:31		Middle	2.5	26.90	26.90		8.27	8.27		31.37	31.37		73.1	74.0		4.90	4.96		2.16	2.15		3	
25/8/2015	9:07	Fine	Middle	2.5	26.20	26.20	26.25	8.36	8.36	8.36	32.15	32.15	32.15	80.7	79.7	80.9	5.43	5.37	5.44	3.50	3.52	3.52	8	8.00
	9:09		Middle	2.5	26.30	26.30		8.36	8.36		32.14	32.14		82.7	80.3		5.57	5.40		3.52	3.52		8	
27/8/2015	9:08	Fine	Middle	2.5	26.20	26.20	26.15	8.28	8.28	8.28	32.74	32.74	32.75	72.4	70.0	70.8	4.88	4.71	4.77	3.37	3.41	3.47	6	5.50
	9:10		Middle	2.5	26.10	26.10		8.28	8.28		32.76	32.76		70.0	70.6		4.72	4.76		3.46	3.63		5	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at P5 - WCT / RT / IT  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids						
					°C		-			ppt		%		mg/L		NTU		mg/L						
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	11:35	Fine	Middle	2.5	27.60	27.60	27.65	8.23	8.23	8.23	24.59	24.59	24.49	84.5	85.7	85.2	5.80	5.88	5.85	1.64	1.64	1.65	5	4.50
	11:37		Middle	2.5	27.70	27.70		8.23	8.23		24.39	24.39		85.8	84.9		5.89	5.82		1.67	1.65		4	
30/7/2015	10:56	Fine	Middle	2.5	27.30	27.30	27.35	8.39	8.39	8.39	26.34	26.34	26.33	81.6	80.9	80.1	5.56	5.51	5.46	2.77	2.75	2.75	2	3.00
	10:58		Middle	2.5	27.40	27.40		8.39	8.39		26.31	26.31		80.0	78.0		5.45	5.31		2.74	2.74		4	
1/8/2015	10:55	Fine	Middle	2.5	26.40	26.40	26.45	8.22	8.22	8.22	29.22	29.22	29.22	69.5	68.0	67.2	4.74	4.63	4.58	2.30	2.29	2.28	2	2.50
	10:57		Middle	2.5	26.50	26.50		8.22	8.22		29.22	29.22		66.4	64.8		4.53	4.42		2.27	2.27		3	
3/8/2015	14:26	Fine	Middle	2.5	26.70	26.70	26.75	8.29	8.29	8.29	29.23	29.23	29.22	78.2	77.8	77.8	5.31	5.28	5.28	2.72	2.73	2.66	4	4.50
	14:28		Middle	2.5	26.80	26.80		8.29	8.29		29.21	29.21		77.8	77.3		5.28	5.25		2.64	2.55		5	
5/8/2015	15:10	Fine	Middle	2.5	26.90	26.90	26.95	8.37	8.37	8.38	29.84	29.84	29.84	78.3	78.0	78.9	5.28	5.26	5.32	2.79	2.83	2.81	5	4.50
	15:12		Middle	2.5	27.00	27.00		8.38	8.38		29.84	29.84		80.1	79.1		5.40	5.33		2.82	2.80		4	
7/8/2015	16:54	Sunny	Middle	2.5	27.70	27.70	27.75	8.51	8.51	8.51	30.43	30.43	30.42	100.0	99.9	99.9	6.63	6.63	6.63	4.01	3.85	3.95	7	7.00
	16:56		Middle	2.5	27.80	27.80		8.51	8.51		30.40	30.40		100.0	99.7		6.63	6.61		3.95	3.97		7	
10/8/2015	9:45	Cloudy	Middle	3.0	26.70	26.70	26.70	8.48	8.48	8.49	30.40	30.40	30.40	96.4	97.1	96.2	6.51	6.56	6.50	3.86	3.85	3.83	5	6.00
	9:47		Middle	3.0	26.70	26.70		8.49	8.49		30.40	30.40		95.6	95.5		6.46	6.45		3.81	3.78		7	
12/8/2015	10:50	Sunny	Middle	2.5	26.80	26.80	26.85	8.37	8.37	8.37	30.72	30.72	30.72	79.2	79.9	79.5	5.33	5.37	5.34	3.79	3.83	3.82	7	6.50
	10:52		Middle	2.5	26.90	26.90		8.37	8.37		30.71	30.71		79.2	79.5		5.32	5.34		3.78	3.87		6	
14/8/2015	11:12	Cloudy	Middle	2.5	26.40	26.40	26.45	8.30	8.30	8.30	30.05	30.05	30.06	72.3	71.4	70.5	4.91	4.85	4.79	3.85	3.97	3.74	5	5.00
	11:14		Middle	2.5	26.50	26.50		8.30	8.30		30.07	30.07		69.3	68.8		4.71	4.67		3.76	3.38		5	
17/8/2015	15:30	Fine	Middle	2.5	27.00	27.00	27.10	8.19	8.19	8.19	30.55	30.55	30.56	76.0	76.1	76.1	5.10	5.11	5.11	4.56	4.67	4.70	5	5.50
	15:32		Middle	2.5	27.20	27.20		8.19	8.19		30.57	30.57		76.0	76.3		5.10	5.12		4.81	4.75		6	
19/8/2015	14:20	Sunny	Middle	2.5	27.60	27.60	27.65	8.20	8.20	8.20	30.40	30.40	30.40	82.8	81.9	81.9	5.51	5.54	5.47	3.23	3.23	3.24	4	4.50
	14:22		Middle	2.5	27.70	27.70		8.20	8.20		30.40	30.40		81.7	81.2		5.43	5.40		3.24	3.24		5	
21/8/2015	16:33	Fine	Middle	2.5	26.60	26.60	26.60	8.28	8.28	8.28	31.42	31.42	31.42	73.4	72.7	73.5	4.94	4.89	4.94	3.97	4.02	3.94	5	4.00
	16:35		Middle	2.5	26.60	26.60		8.28	8.28		31.42	31.42		73.3	74.4		4.93	5.00		4.01	3.76		3	
25/8/2015	9:11	Fine	Middle	2.5	26.00	26.00	26.05	8.37	8.37	8.37	32.14	32.14	32.16	81.0	78.2	77.7	5.48	5.29	5.25	4.15	4.01	4.05	9	8.50
	9:13		Middle	2.5	26.10	26.10		8.37	8.37		32.17	32.17		76.3	75.2		5.16	5.08		4.02	4.00		8	
27/8/2015	9:12	Fine	Middle	2.5	26.20	26.20	26.18	8.28	8.28	8.28	32.77	32.77	32.77	71.2	69.6	69.4	4.78	4.67	4.66	4.68	4.68	4.71	5	5.50
	9:14		Middle	2.5	26.00	26.30		8.28	8.28		32.77	32.77		69.0	67.9		4.64	4.53		4.73	4.75		6	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at RW21-P789 - Sun Hung Kai Centre  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids						
					°C		-		ppt		%		mg/L		NTU		mg/L							
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	8:35	Fine	Middle	3.5	27.10	27.10	27.15	7.96	7.96	7.98	26.36	26.36	26.36	77.2	76.9	76.7	5.29	5.28	5.26	1.32	1.30	1.29	4	3.50
	8:37		Middle	3.5	27.20	27.20		7.99	7.99		26.36	26.36		77.3	75.3		5.30	5.16		1.28	1.26		3	
30/7/2015	11:17	Fine	Middle	3.5	26.80	26.80	26.95	8.33	8.33	8.34	27.61	27.61	27.59	83.3	78.7	79.7	5.49	5.38	5.42	4.20	4.07	4.08	9	9.50
	11:19		Middle	3.5	27.10	27.10		8.34	8.34		27.57	27.57		77.5	79.1		5.38	5.41		4.03	4.01		10	
1/8/2015	11:19	Fine	Middle	3.5	26.20	26.20	26.25	8.15	8.15	8.17	30.45	30.45	30.43	72.1	74.9	74.1	4.90	5.09	5.03	2.35	2.43	2.40	4	4.00
	11:21		Middle	3.5	26.30	26.30		8.18	8.18		30.41	30.41		75.2	74.0		5.11	5.03		2.44	2.37		4	
3/8/2015	14:54	Fine	Middle	3.5	26.60	26.60	26.65	8.22	8.22	8.23	29.98	29.98	29.96	72.3	71.5	71.7	4.90	4.85	4.86	3.14	3.11	3.09	3	3.50
	14:56		Middle	3.5	26.70	26.70		8.24	8.24		29.93	29.93		71.4	71.7		4.84	4.83		3.07	3.05		4	
5/8/2015	15:32	Fine	Middle	3.5	26.80	26.80	26.90	8.34	8.34	8.36	30.20	30.20	30.18	78.9	78.9	81.5	5.31	5.31	5.47	2.98	2.98	2.90	5	5.00
	15:34		Middle	3.5	27.00	27.00		8.37	8.37		30.15	30.15		86.2	82.0		5.75	5.52		2.87	2.77		5	
7/8/2015	17:10	Sunny	Middle	3.5	27.50	27.50	27.60	8.47	8.47	8.48	30.51	30.51	30.50	95.3	94.2	93.9	6.34	6.26	6.24	4.30	4.30	4.22	7	6.50
	17:12		Middle	3.5	27.70	27.70		8.48	8.48		30.49	30.49		92.4	93.8		6.14	6.23		4.22	4.05		6	
10/8/2015	10:00	Cloudy	Middle	3.5	26.70	26.70	26.70	8.43	8.43	8.43	30.55	30.55	30.55	89.6	90.9	90.7	6.04	6.13	6.12	3.54	3.52	3.55	5	5.00
	10:02		Middle	3.5	26.70	26.70		8.43	8.43		30.55	30.55		91.2	91.1		6.15	6.14		6.12	3.51		3.61	
12/8/2015	11:09	Sunny	Middle	3.5	26.60	26.60	26.70	8.31	8.31	8.32	31.34	31.33	31.32	79.9	79.3	77.8	5.37	5.32	5.22	3.37	3.24	3.25	5	5.50
	11:11		Middle	3.5	26.80	26.80		8.32	8.32		31.31	31.31		76.7	75.2		5.15	5.05		3.19	3.18		6	
14/8/2015	11:25	Cloudy	Middle	3.5	26.00	26.00	26.05	8.28	8.28	8.28	30.43	30.43	30.42	75.5	75.2	73.9	5.16	5.14	5.05	6.80	6.73	6.73	9	9.50
	11:27		Middle	3.5	26.10	26.10		8.28	8.28		30.40	30.40		73.1	71.8		4.99	4.90		6.71	6.68		10	
17/8/2015	15:45	Fine	Middle	3.0	27.30	27.30	27.40	8.13	8.13	8.13	30.62	30.62	30.62	66.2	66.0	65.2	4.41	4.40	4.35	5.64	5.87	5.74	7	6.00
	15:47		Middle	3.0	27.50	27.50		8.13	8.13		30.62	30.62		64.6	64.1		4.30	4.27		5.89	5.55		5	
19/8/2015	14:30	Sunny	Middle	3.0	26.90	26.90	27.00	8.18	8.18	8.18	31.01	31.01	31.01	82.5	82.3	82.1	5.53	5.51	5.53	2.76	2.75	2.75	6	5.50
	14:32		Middle	3.0	27.10	27.10		8.18	8.18		31.00	31.00		82.7	81.0		5.54	5.52		2.75	2.75		5	
21/8/2015	14:18	Fine	Middle	3.5	26.90	26.90	27.10	8.22	8.22	8.21	31.95	31.95	31.90	74.7	74.7	74.5	4.97	4.97	4.95	3.34	3.29	3.30	3	3.50
	14:20		Middle	3.5	27.30	27.30		8.20	8.20		31.84	31.84		74.6	73.8		4.96	4.91		3.29	3.26		4	
25/8/2015	9:24	Fine	Middle	3.5	26.30	26.30	26.35	8.26	8.26	8.26	32.54	32.54	32.51	70.1	69.2	70.6	4.71	4.64	4.74	4.33	4.22	4.24	6	7.00
	9:26		Middle	3.5	26.40	26.40		8.26	8.26		32.47	32.47		71.1	71.9		4.77	4.82		4.20	4.21		8	
27/8/2015	9:28	Fine	Middle	3.5	26.00	26.00	26.05	8.28	8.28	8.29	33.02	33.02	33.01	70.5	72.8	72.5	4.75	4.90	4.88	3.81	3.81	3.82	4	4.00
	9:30		Middle	3.5	26.10	26.10		8.29	8.29		33.00	32.99		73.7	73.0		4.96	4.91		3.81	3.83		4	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.






**Water Monitoring Result at WSD19 - Sheung Wan  
Mid-Ebb Tide**

Date	Time	Weather Condition	Sampling Depth		Water Temperature		pH			Salinity		DO Saturation		DO		Turbidity		Suspended Solids						
					°C		-			ppt		%		mg/L		NTU		mg/L						
					Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average	Value	Average				
28/7/2015	9:40	Fine	Middle	3.5	27.80	27.80	27.85	8.16	8.16	8.17	24.34	24.34	24.35	85.5	83.3	82.5	5.86	5.71	5.65	2.36	2.37	2.37	5	6.00
	9:42		Middle	3.5	27.90	27.90		8.18	8.18		24.35	24.35		80.5	80.5		5.51	5.51		2.37	2.37		7	
30/7/2015	10:05	Fine	Middle	3.5	26.90	26.90	26.95	8.10	8.10	8.16	26.68	26.68	26.68	84.3	84.7	83.5	5.79	5.81	5.73	1.21	1.19	1.18	3	3.00
	10:07		Middle	3.5	27.00	27.00		8.21	8.21		26.68	26.68		83.4	81.7		5.72	5.60		1.17	1.16		3	
1/8/2015	10:07	Fine	Middle	4.0	26.70	26.70	26.75	8.17	8.17	8.18	28.66	28.66	28.66	86.2	86.6	85.7	5.87	5.90	5.84	2.14	2.20	2.19	3	3.50
	10:09		Middle	4.0	26.80	26.80		8.19	8.19		28.65	28.65		85.4	84.5		5.82	5.75		2.20	2.20		4	
3/8/2015	13:35	Fine	Middle	3.5	27.90	27.90	28.10	8.29	8.29	8.28	28.98	28.98	28.99	67.8	67.0	66.4	4.51	4.45	4.43	2.80	2.77	2.77	3	3.00
	13:37		Middle	3.5	28.30	28.30		8.27	8.27		28.99	28.99		65.9	64.9		4.43	4.31		2.76	2.75		3	
5/8/2015	14:10	Fine	Middle	3.5	27.80	27.80	28.05	8.38	8.37	8.36	30.02	30.02	30.07	82.0	78.9	80.5	5.38	5.17	5.29	2.70	2.70	2.63	5	4.50
	14:12		Middle	3.5	28.30	28.30		8.35	8.35		30.11	30.11		80.4	80.7		5.30	5.32		2.57	2.54		4	
7/8/2015	15:55	Sunny	Middle	3.5	28.60	28.60	28.75	8.49	8.49	8.52	29.62	29.62	29.63	119.4	119.6	118.4	7.82	7.83	7.74	4.28	4.29	4.31	5	5.00
	15:57		Middle	3.5	28.90	28.90		8.54	8.54		29.63	29.63		120.0	114.5		7.85	7.45		4.33	4.35		5	
10/8/2015	8:27	Cloudy	Middle	4.0	26.70	26.70	26.70	8.51	8.51	8.50	30.21	30.21	30.21	85.5	85.0	84.2	5.78	5.75	5.71	3.75	3.75	3.75	4	4.50
	8:29		Middle	4.0	26.70	26.70		8.48	8.48		30.21	30.21		83.1	83.3		5.66	5.63		3.74	3.74		5	
12/8/2015	9:51	Sunny	Middle	3.5	27.10	27.10	27.25	8.37	8.37	8.36	30.96	30.96	30.93	72.7	73.3	72.4	4.85	4.89	4.83	4.56	4.80	4.76	6	5.50
	9:53		Middle	3.5	27.40	27.40		8.35	8.35		30.89	30.89		72.4	71.0		4.83	4.74		4.84	4.85		5	
14/8/2015	10:01	Cloudy	Middle	3.5	25.90	25.90	25.95	8.28	8.28	8.29	30.32	30.32	30.32	62.9	32.5	54.4	4.30	4.27	4.23	3.87	3.81	3.80	5	5.00
	10:03		Middle	3.5	26.00	26.00		8.29	8.29		30.32	30.32		61.4	60.7		4.20	4.15		3.76	3.77		5	
17/8/2015	14:25	Fine	Middle	3.0	28.80	28.80	28.95	8.28	8.28	8.24	30.21	30.21	30.18	74.7	73.5	73.3	4.90	4.80	4.77	9.07	9.06	9.13	6	6.00
	14:27		Middle	3.0	29.10	29.10		8.19	8.19		30.15	30.15		73.1	72.0		4.77	4.60		9.10	9.29		6	
19/8/2015	13:20	Sunny	Middle	3.0	28.00	28.00	28.20	8.27	8.27	8.25	30.56	30.56	30.56	80.8	81.1	80.7	5.32	5.33	5.30	3.03	3.03	3.03	3	3.00
	13:22		Middle	3.0	28.40	28.40		8.22	8.22		30.55	30.55		80.2	80.6		5.27	5.29		3.04	3.03		3	
21/8/2015	15:26	Fine	Middle	3.5	27.10	27.10	27.20	8.10	8.10	8.14	31.18	31.18	31.11	75.8	76.4	75.2	5.06	5.10	5.02	3.86	3.56	3.62	3	3.50
	15:28		Middle	3.5	27.30	27.30		8.18	8.18		31.04	31.04		75.0	73.7		5.00	4.92		3.54	3.52		4	
25/8/2015	8:13	Fine	Middle	3.5	26.30	26.30	26.40	8.41	8.41	8.39	32.23	32.24	32.22	69.1	67.8	67.5	4.64	4.56	4.53	6.95	6.88	6.99	4	4.50
	8:15		Middle	3.5	26.50	26.50		8.37	8.37		32.21	32.21		67.0	65.9		4.50	4.42		7.07	7.05		5	
27/8/2015	8:00	Fine	Middle	3.5	26.20	26.20	26.25	8.24	8.24	8.24	32.84	32.84	32.85	56.1	56.4	56.5	3.76	3.78	3.78	4.71	4.80	4.80	4	5.00
	8:02		Middle	3.5	26.30	26.30		8.20	8.26		32.85	32.85		56.7	56.9		3.80	3.78		4.84	4.85		6	

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.






# Graphic Presentation of Water Quality Result of WSD19 - Sheung Wan

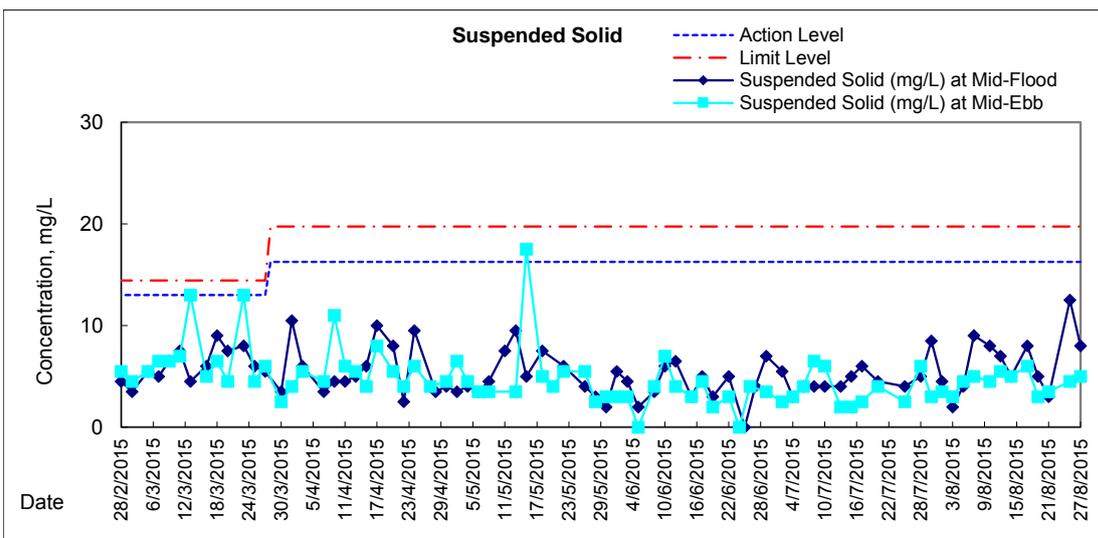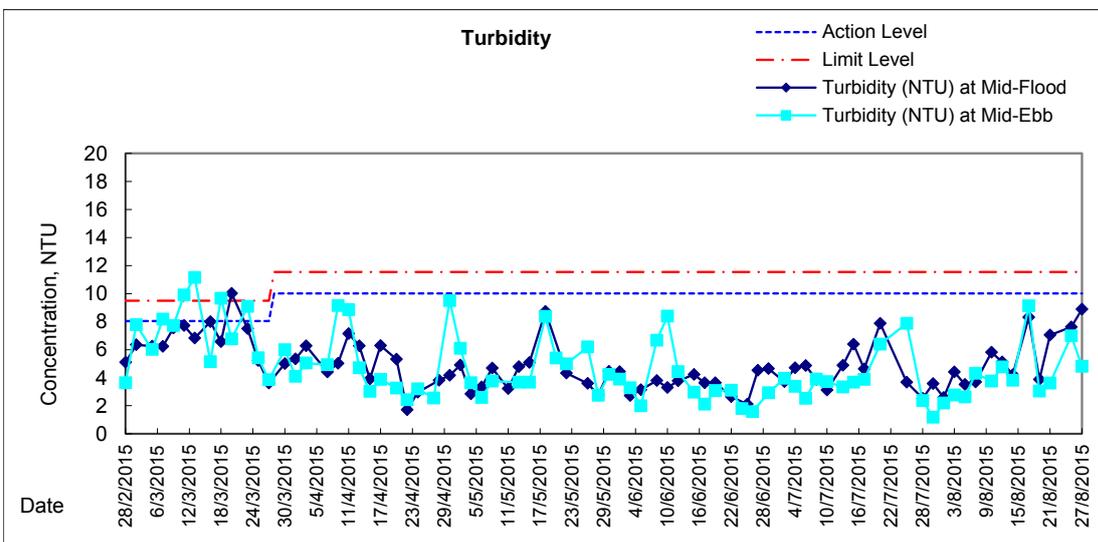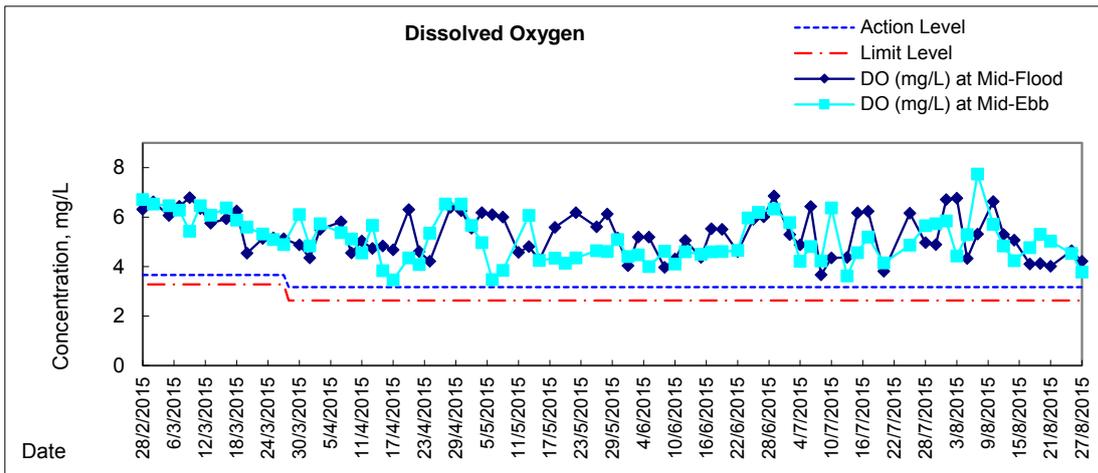






### Graphic Presentation of Water Quality Result of C1 - HKCEC

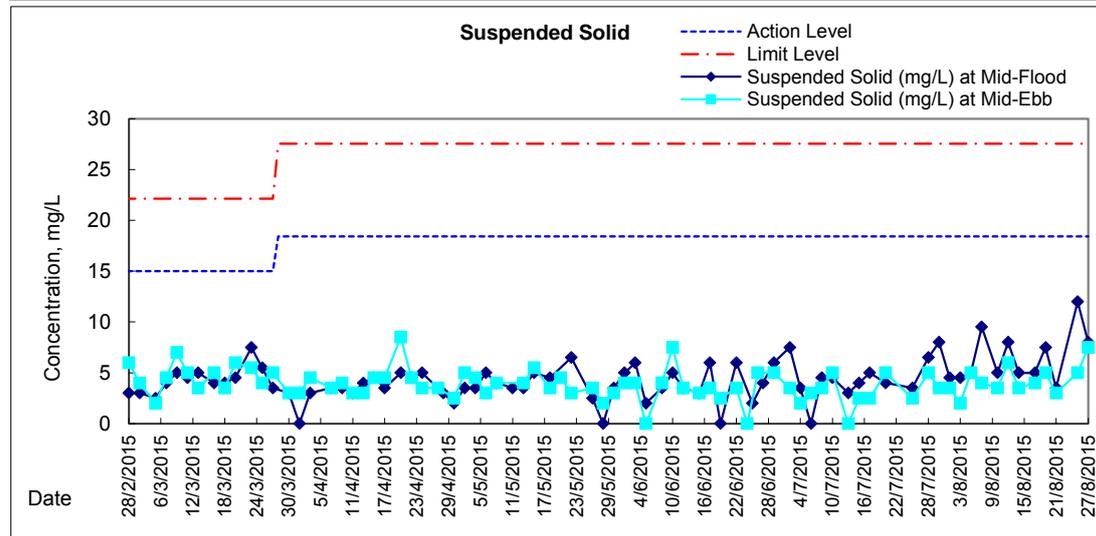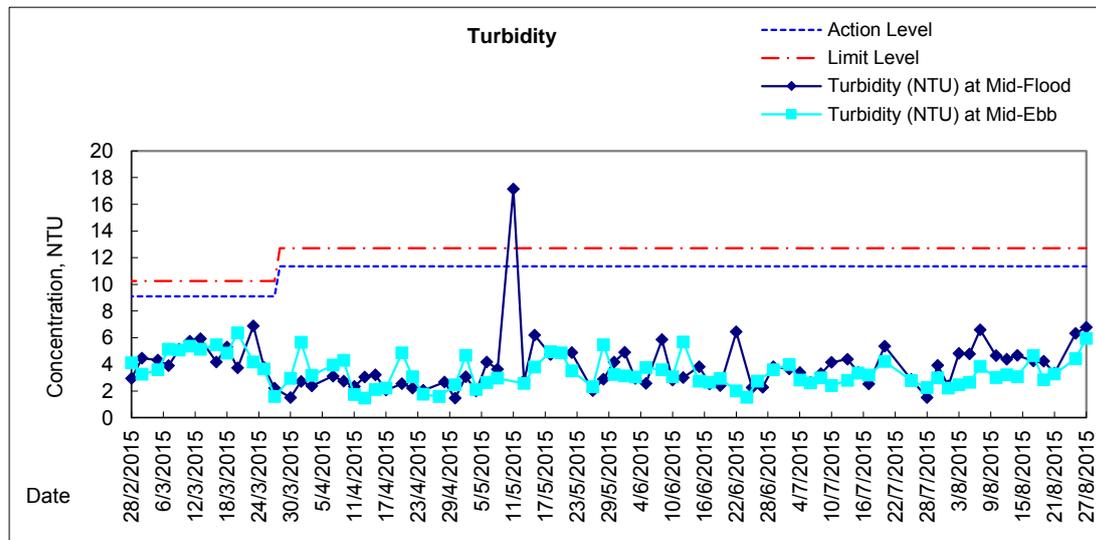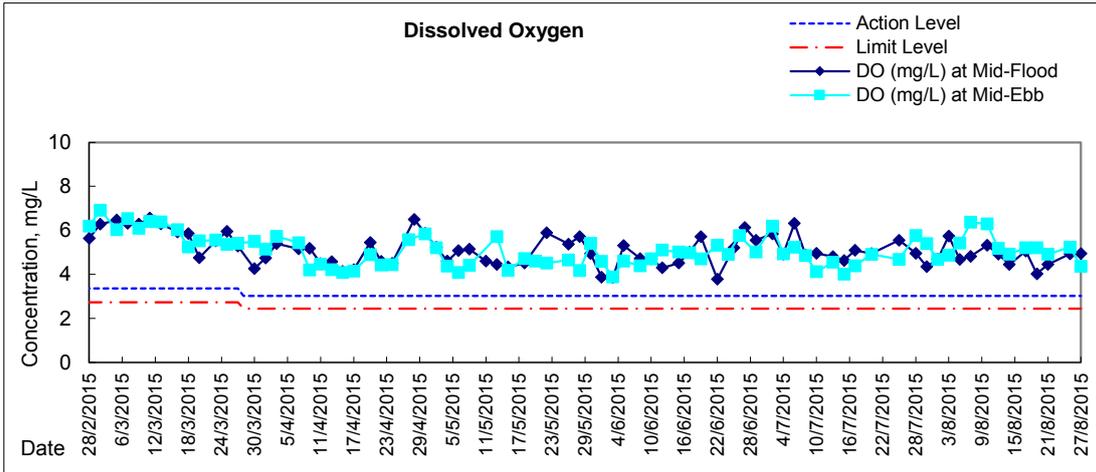






# Graphic Presentation of Water Quality Result of P1 - HKCEC Phase I

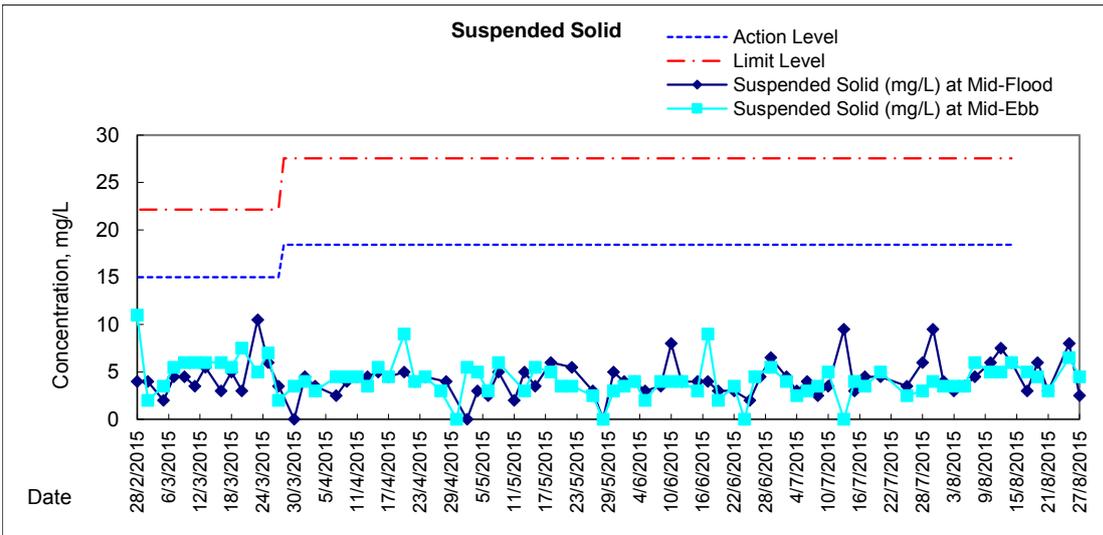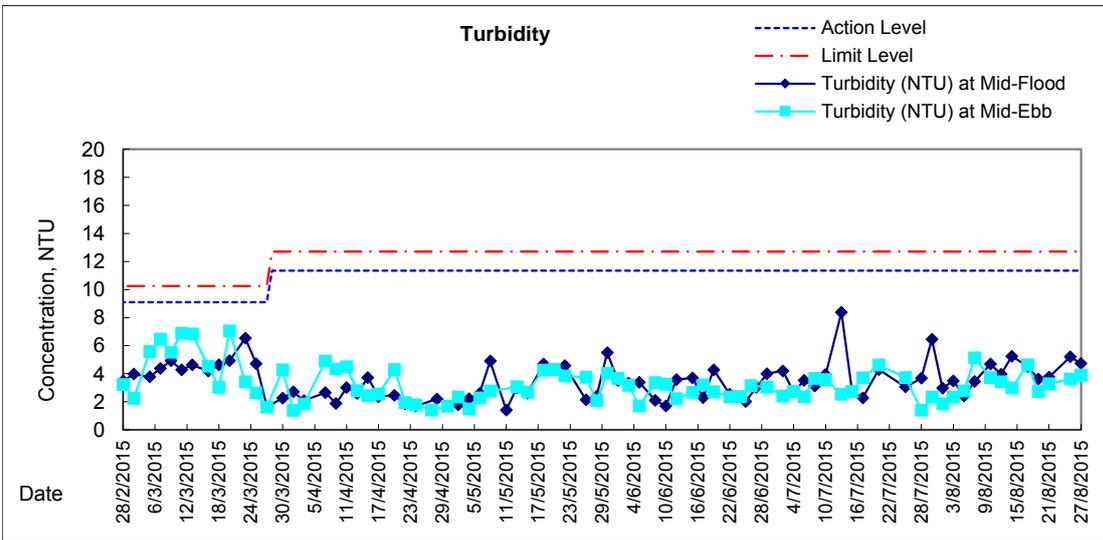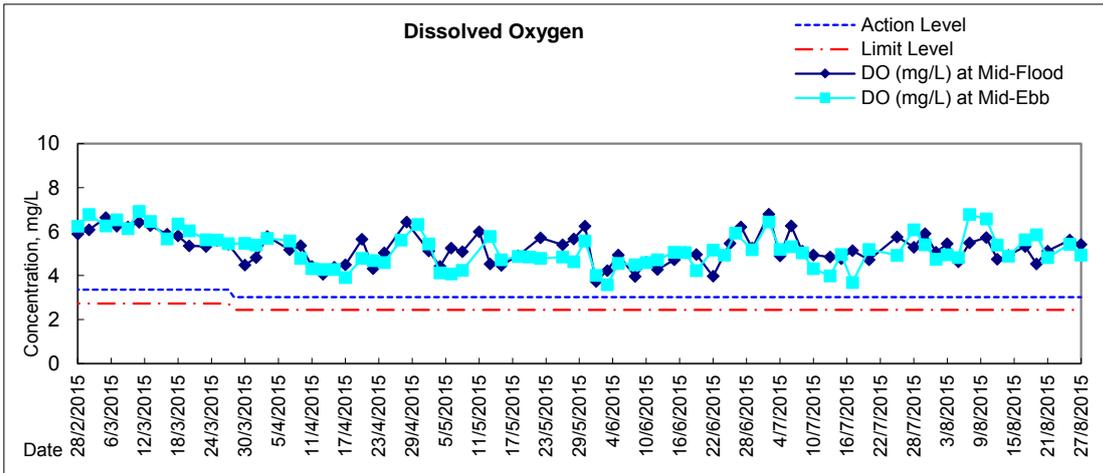






# Graphic Presentation of Water Quality Result of P3 - APA

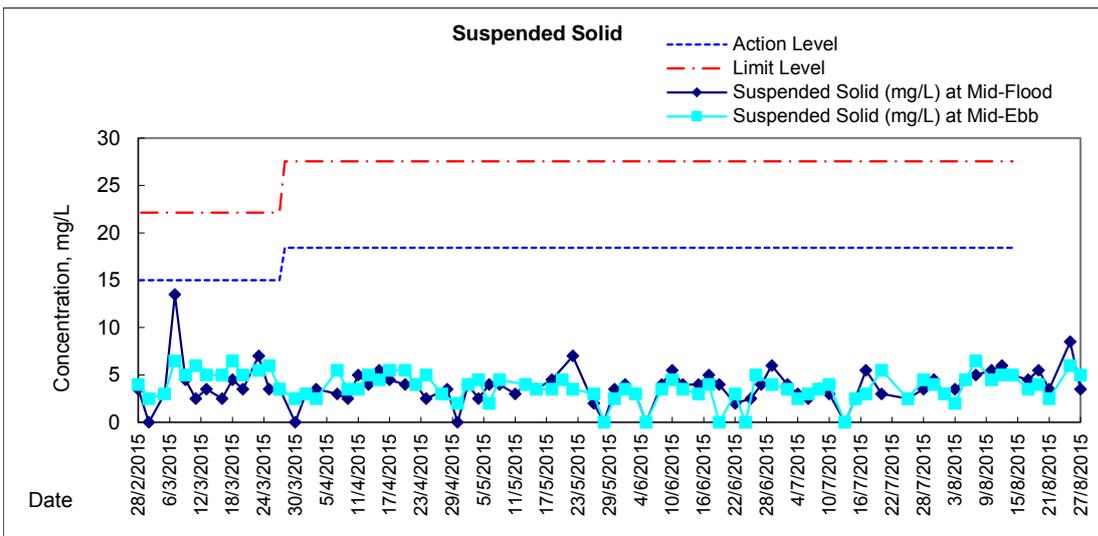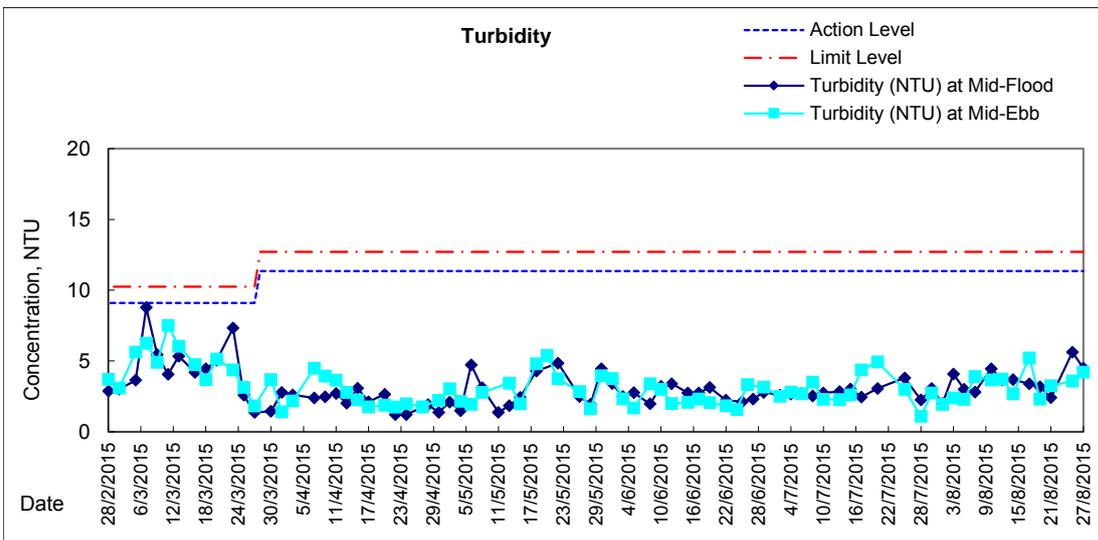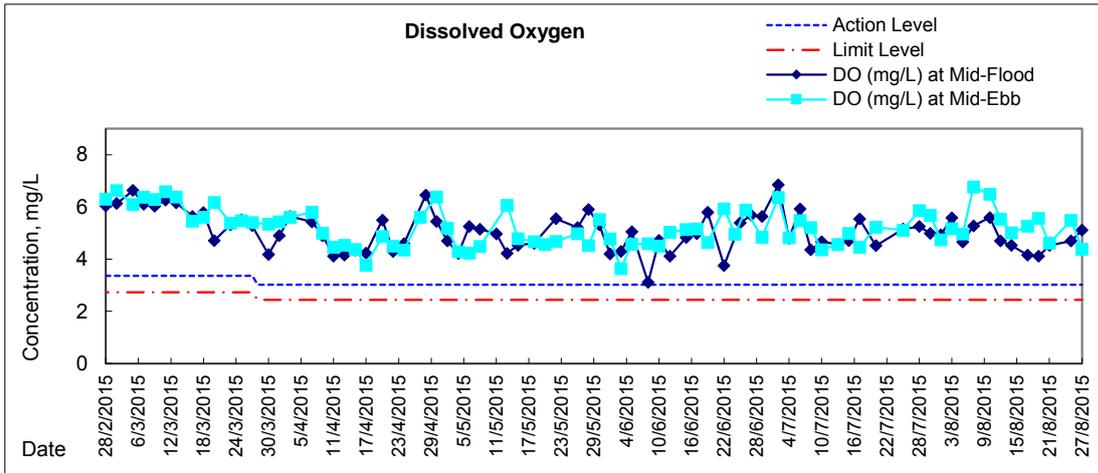






### Graphic Presentation of Water Quality Result of P5 - WCT / RT / IT

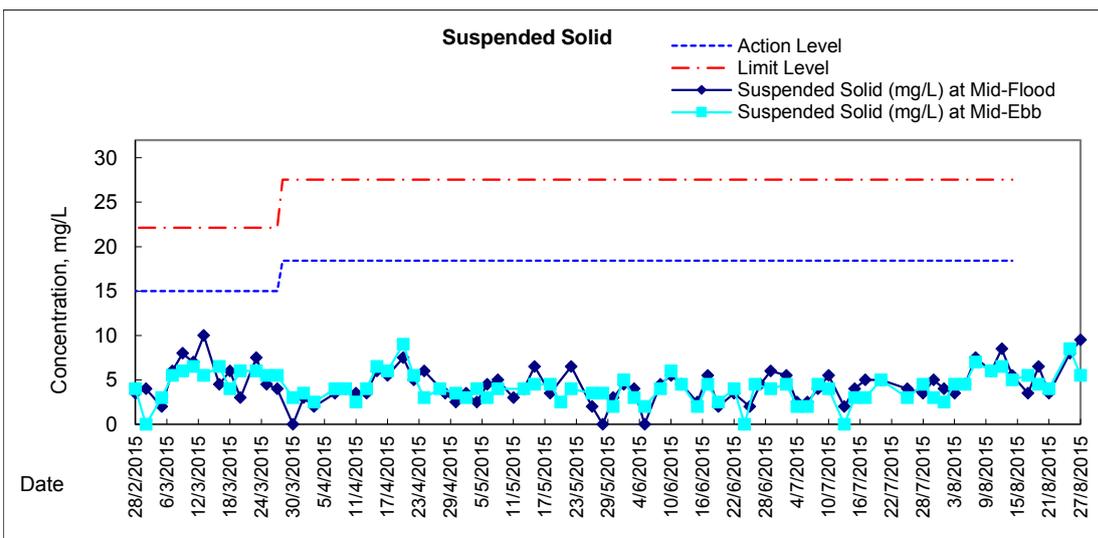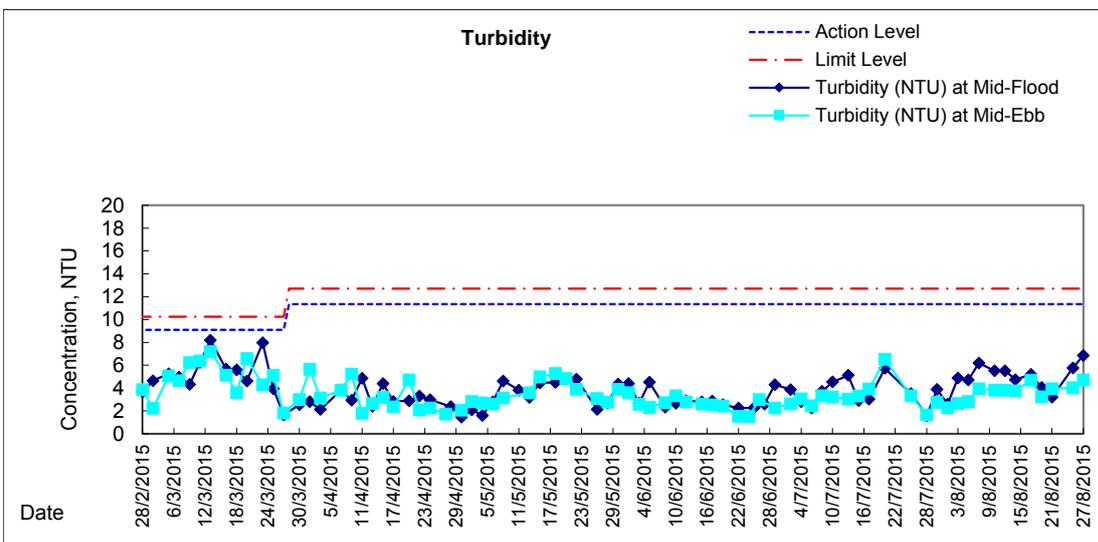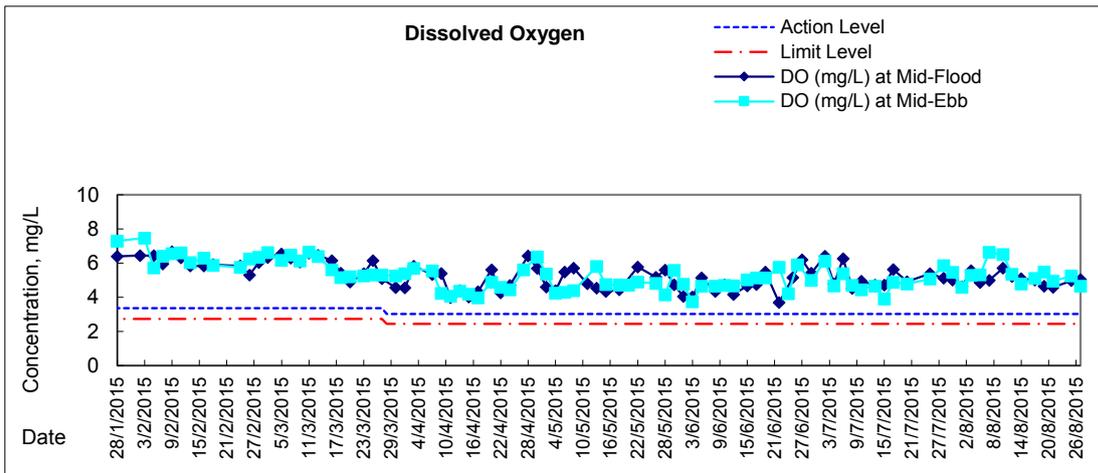






### Graphic Presentation of Water Quality Result of P4 - SOC

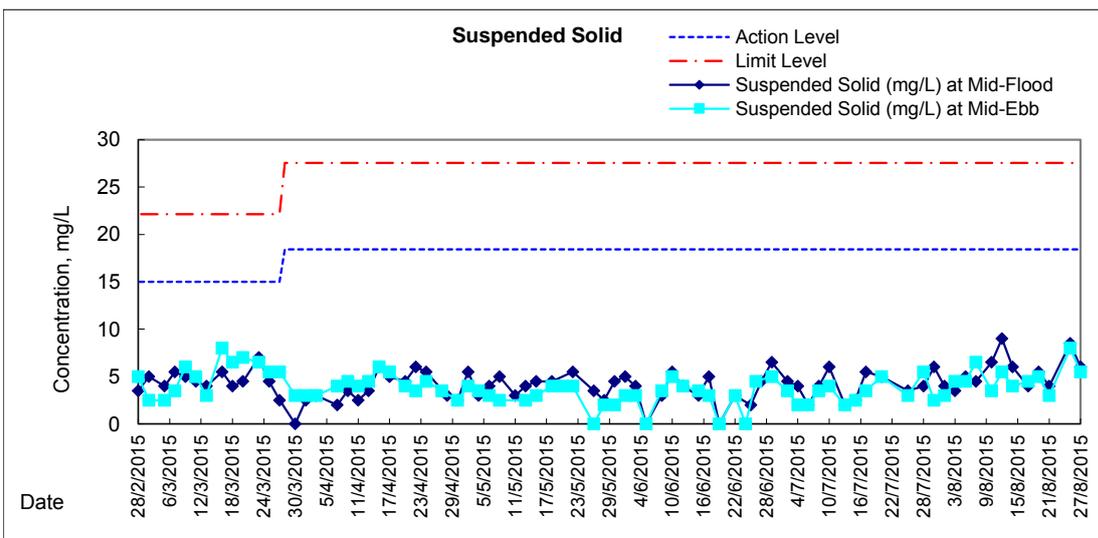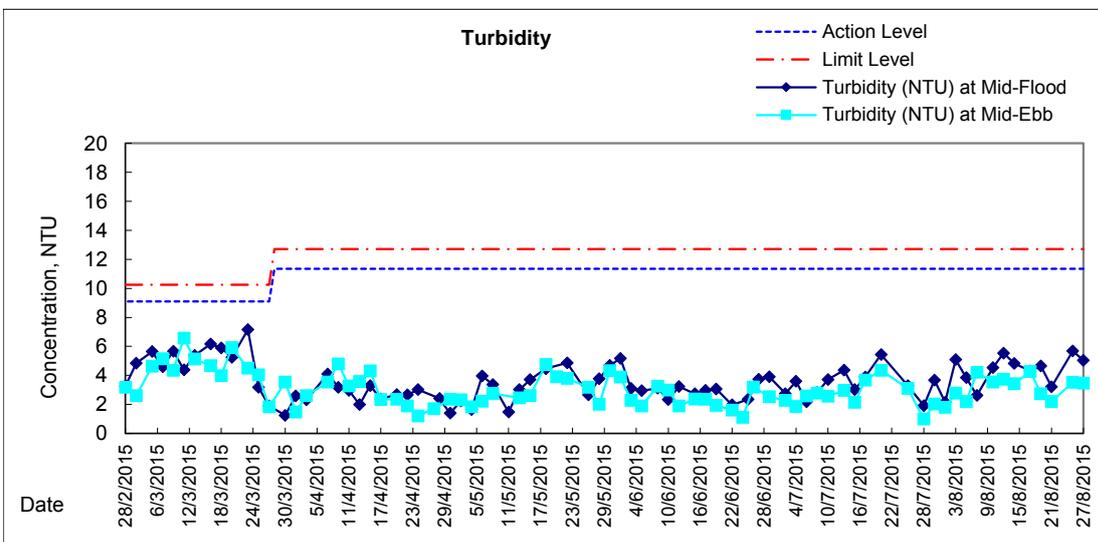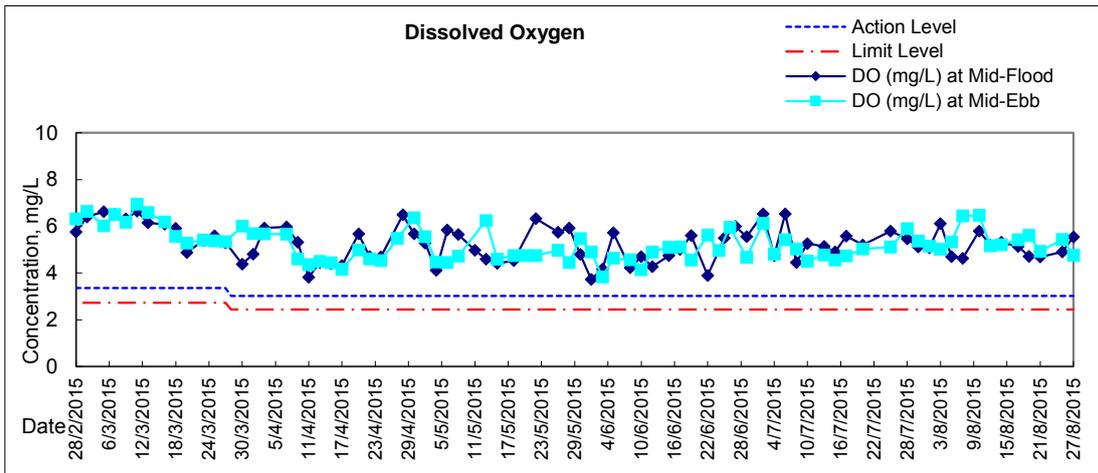






# Graphic Presentation of Water Quality Result of RW21-P789 - GEC/CRC/SHK

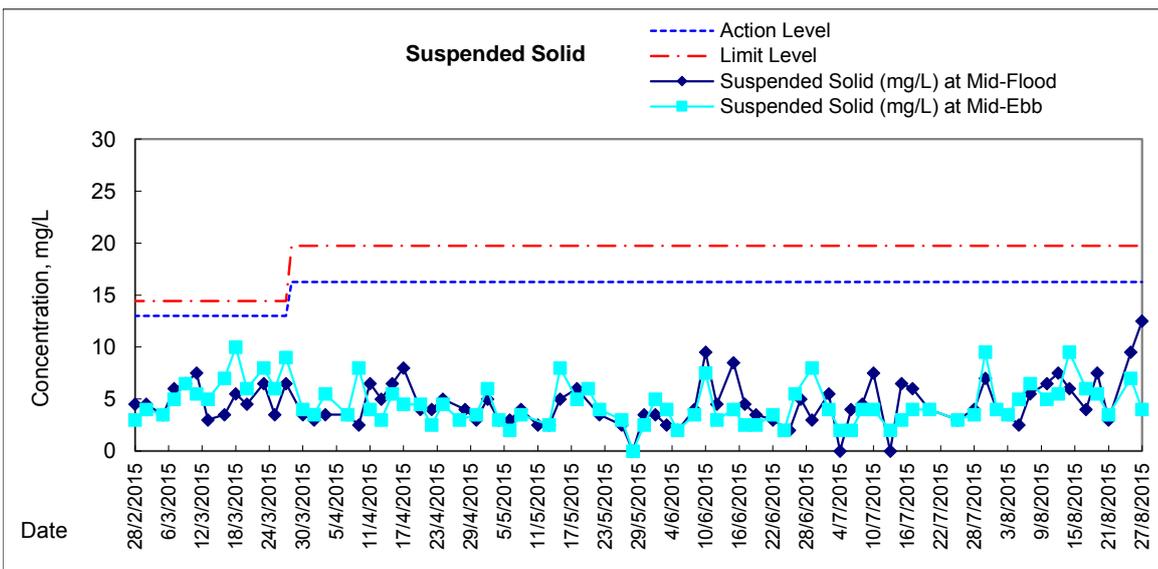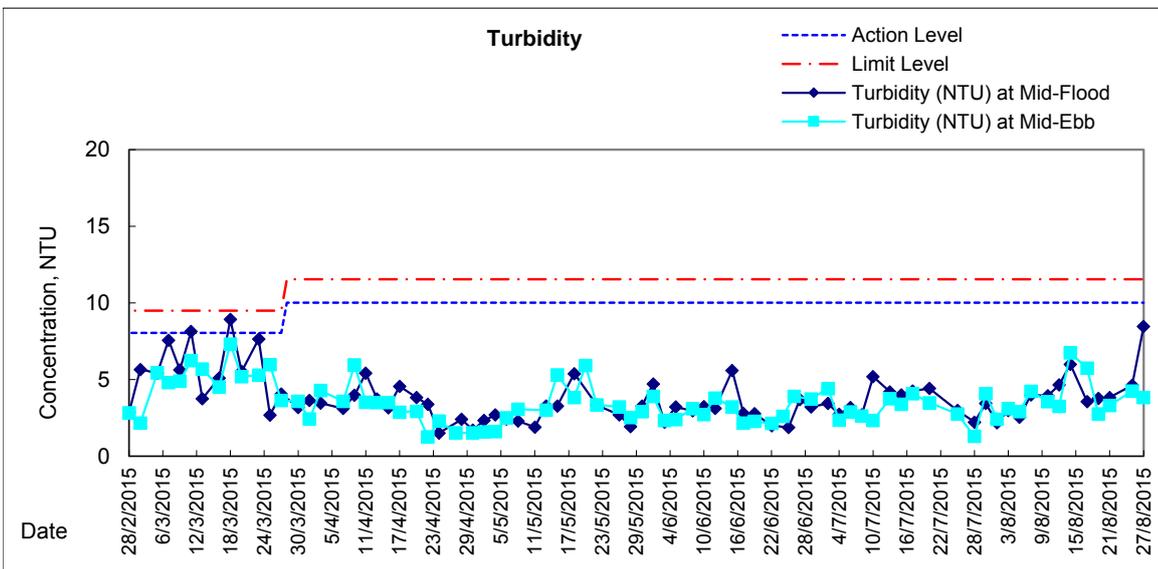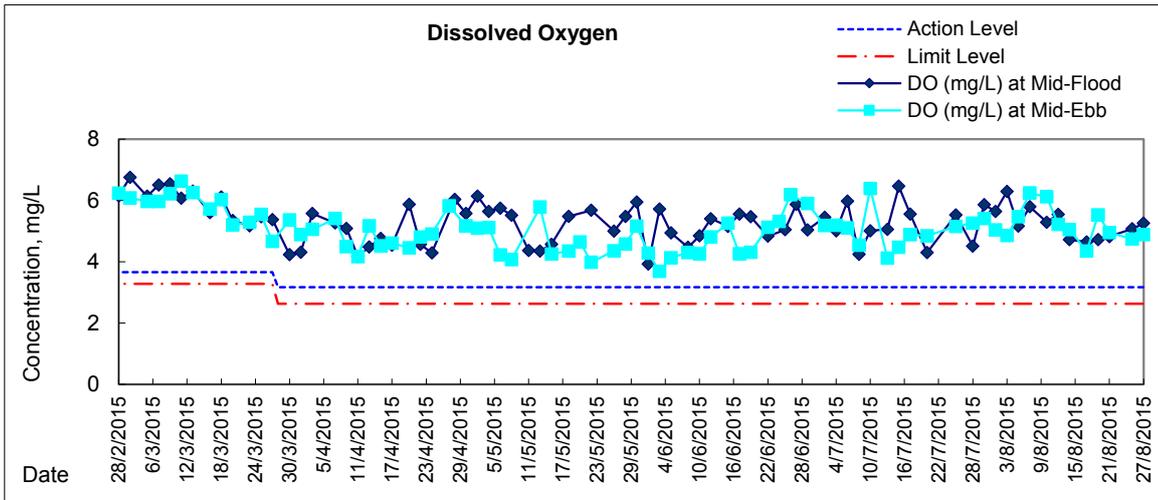



### Graphic Presentation of Water Quality Result of C7 - Windsor House

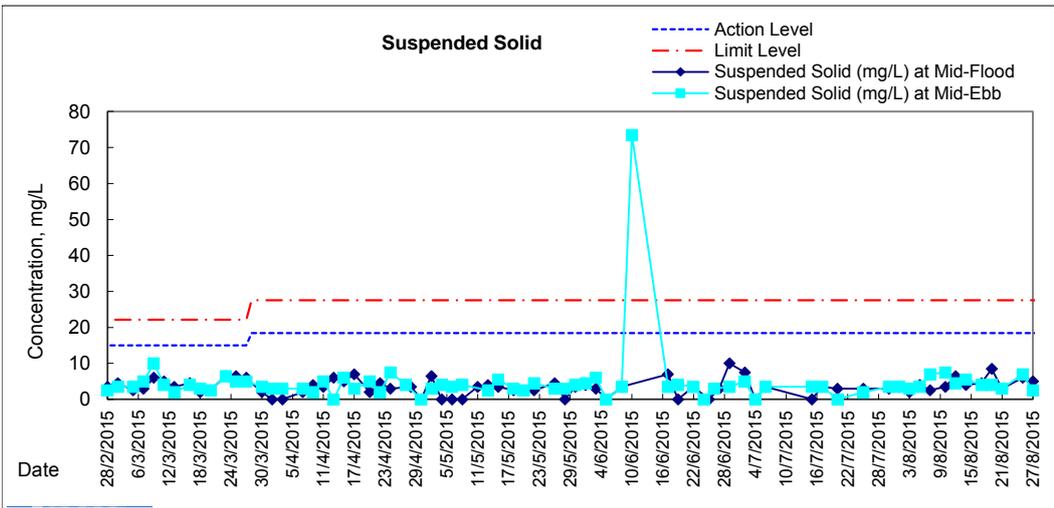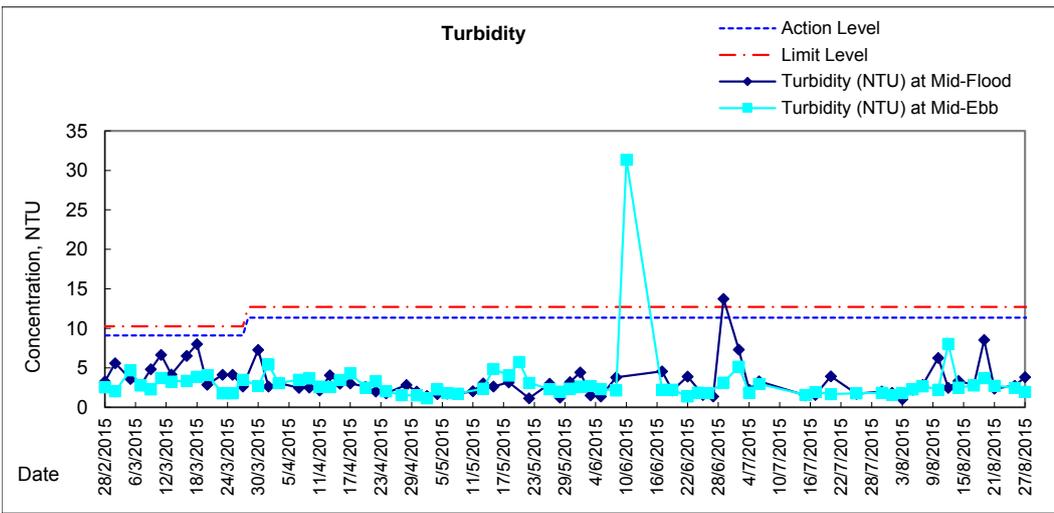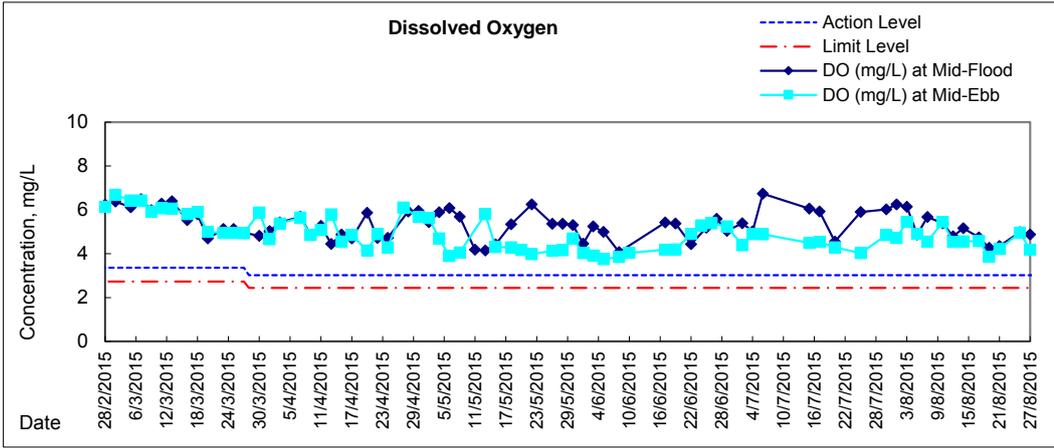



**Water Monitoring Result at C6 - Excelsior Hotel  
Mid-Flood Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature			pH			Salinity			DO Saturation			DO		
					°C			-			ppt			%			mg/L		
					Value	Average		Value	Average		Value	Average		Value	Average		Value	Average	
28/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	17:50		Middle	1.5	27.70	27.70	27.7	8.10	8.10	8.1	25.34	25.34	25.3	65.3	64.7	65.0	4.43	4.42	4.43
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30/7/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	18:50		Middle	1.5	26.50	26.50	26.5	8.30	8.30	8.3	26.97	26.97	27.0	77.1	77.0	77.1	5.33	5.33	5.33
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
1/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	21:50		Middle	1.5	25.64	25.62	25.6	7.50	7.49	7.5	27.41	27.41	27.4	69.8	69.1	69.5	4.97	4.92	4.95
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
3/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	19:50		Middle	1.5	26.47	26.47	26.5	7.47	7.47	7.5	28.20	28.20	28.2	97.6	96.9	97.3	6.70	6.65	6.68
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
5/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	10:33		Middle	1.5	26.70	26.70	26.7	8.19	8.19	8.2	29.14	29.14	29.1	73.7	72.6	73.2	5.01	4.94	4.98
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7/8/2015	-	Fine	Surface	-	-	-	-	0.00	-	0.0	-	-	-	-	-	-	-	-	-
	12:40		Middle	1.5	27.00	27.00	27.0	8.21	8.21	8.2	29.40	29.40	29.4	71.7	72.2	72.0	4.84	4.88	4.86
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
10/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	13:26		Middle	1.0	27.70	27.70	27.7	8.39	8.39	8.4	29.52	29.52	29.5	91.4	89.6	90.5	6.09	5.97	6.03
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
12/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	15:10		Middle	1.0	29.00	29.00	29.0	8.27	8.27	8.3	30.33	30.33	30.3	68.7	69.8	69.3	4.44	4.51	4.48
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	18:45		Middle	1.0	25.70	25.70	25.7	8.16	8.16	8.2	28.09	28.09	28.1	63.7	64.4	64.1	4.45	4.48	4.47
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
17/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	10:22		Middle	1.0	26.80	26.80	26.8	8.08	8.08	8.1	30.02	30.02	30.0	75.2	75.5	75.4	5.06	5.07	5.07
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
19/8/2015	9:46	Fine	Surface	1.0	27.20	27.20	27.2	8.07	8.07	8.1	27.86	27.86	27.9	66.8	67.6	67.2	4.53	4.58	4.56
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:48		Bottom	3.0	26.70	26.70	26.7	8.04	8.04	8.0	29.96	29.96	30.0	67.8	66.5	67.2	4.58	4.49	4.54
21/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:53		Middle	1.5	26.60	26.60	26.6	8.08	8.08	8.1	29.84	29.84	29.8	57.7	58.9	58.3	3.91	3.99	3.95
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
25/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	16:45		Middle	1.0	27.50	27.50	27.5	8.21	8.21	8.2	29.99	29.99	30.0	71.5	70.9	71.2	4.77	4.73	4.75
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
27/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	17:45		Middle	1.5	26.50	26.50	26.5	8.22	8.22	8.2	31.94	31.94	31.9	63.8	64.1	64.0	4.29	4.31	4.30
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at Ex-WPCWA SW - South-western corners of ex-Public Cargo Works Area  
Mid-Flood Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature			pH			Salinity			DO Saturation			DO		
					°C			-			ppt			%			mg/L		
					Value	Average		Value	Average		Value	Average		Value	Average		Value	Average	
28/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	16:40		Middle	1.5	27.30	27.30	27.3	8.16	8.16	8.2	25.33	25.33	25.3	53.0	51.9	52.5	3.64	3.56	3.60
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30/7/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	17:26		Middle	1.5	26.80	26.80	26.8	8.42	8.42	8.4	17.79	17.79	17.8	58.6	58.0	58.3	4.24	4.20	4.22
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
1/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	21:19		Middle	1.5	25.38	25.38	25.4	7.43	7.43	7.4	20.01	19.93	20.0	47.5	47.0	47.3	3.55	3.50	3.53
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
3/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	20:28		Middle	1.0	26.70	26.70	26.7	7.55	7.55	7.6	16.82	16.82	16.8	73.2	73.1	73.2	5.34	5.33	5.34
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
5/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	10:18		Middle	1.0	26.10	26.10	26.1	8.26	8.26	8.3	29.02	29.02	29.0	61.5	61.3	61.4	4.23	4.21	4.22
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:30		Middle	1.0	27.20	27.20	27.2	8.31	8.31	8.3	23.84	23.84	23.8	63.8	64.0	63.9	4.43	4.44	4.44
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
10/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	16:55		Middle	1.0	26.60	26.60	26.6	8.35	8.35	8.4	26.56	26.56	26.6	55.7	55.0	55.4	3.85	3.80	3.83
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
12/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	18:25		Middle	1.0	26.90	26.90	26.9	8.23	8.23	8.2	29.32	29.32	29.3	56.8	56.5	56.7	3.34	3.32	3.33
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	21:36		Middle	1.0	25.60	25.60	25.6	8.02	8.02	8.0	23.41	23.41	23.4	41.6	41.9	41.8	2.97	2.99	<u>2.98</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
17/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:35		Middle	1.5	25.90	25.90	25.9	8.15	8.15	8.2	29.90	29.90	29.9	60.8	60.4	60.6	4.16	4.14	4.15
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
19/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:28		Middle	1.0	26.20	26.20	26.2	8.08	8.08	8.1	29.20	29.20	29.2	57.3	57.0	57.2	3.91	3.89	3.90
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:25		Middle	1.0	26.50	26.50	26.5	8.14	8.14	8.1	29.87	29.87	29.9	66.9	66.2	66.6	4.53	4.46	4.50
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
25/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	16:27		Middle	1.0	26.10	26.10	26.1	8.29	8.29	8.3	30.91	30.91	30.9	74.7	74.3	74.5	5.07	5.04	5.06
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
27/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	17:00		Middle	1.0	26.30	26.30	26.3	8.25	8.25	8.3	31.49	31.49	31.5	53.0	50.3	51.7	3.58	3.39	3.49
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at Ex-WPCWA SE - South-eastern corners of ex-Public Cargo Works Area  
Mid-Flood Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature			pH			Salinity		DO Saturation		DO				
					°C			-			ppt		%		mg/L				
					Value	Average		Value	Average		Value	Average	Value	Average	Value	Average			
28/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30/7/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
1/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
3/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
5/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
10/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	16:50		Middle	0.5	26.90	26.90	26.9	8.39	8.39	8.4	28.85	28.85	28.9	56.6	56.5	56.6	3.73	3.72	3.73
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
12/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	18:20		Middle	0.5	27.20	27.20	27.2	8.28	8.28	8.3	29.09	29.09	29.1	55.6	55.8	55.7	3.75	3.77	3.76
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	21:25		Middle	0.5	25.30	25.30	25.3	8.20	8.20	8.2	28.96	28.96	29.0	62.1	60.2	61.2	4.34	4.28	4.31
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
17/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:30		Middle	1.0	26.10	26.10	26.1	8.17	8.17	8.2	30.12	30.12	30.1	58.0	59.1	58.6	3.94	4.01	3.98
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
19/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:26		Middle	0.5	26.90	26.90	26.9	8.10	8.10	8.1	29.39	29.39	29.4	45.1	44.0	44.6	3.05	2.98	<u>3.02</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:35		Middle	1.0	26.50	26.50	26.5	8.16	8.16	8.2	29.35	29.35	29.4	51.8	52.9	52.4	3.53	3.60	3.57
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
25/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	16:25		Middle	0.5	26.70	26.70	26.7	8.26	8.26	8.3	31.21	31.21	31.2	61.7	60.4	61.1	4.15	4.05	4.10
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
27/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	17:02		Middle	0.5	26.20	26.20	26.2	8.24	8.24	8.2	30.44	30.44	30.4	48.4	48.6	48.5	3.29	3.31	<u>3.30</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at C6 - Excelsior Hotel  
Mid-Ebb Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature			pH			Salinity			DO Saturation			DO			
					°C			-			ppt			%			mg/L			
					Value	Average		Value	Average		Value	Average		Value	Average		Value	Average		
28/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	9:00		Middle	2	27.40	27.40	27.4	8.05	8.05	8.1	24.58	24.58	24.6	68.7	68.8	68.8	4.73	4.73	4.73	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:38		Middle	2	27.30	27.30	27.3	8.17	8.17	8.2	24.75	24.75	24.8	70.3	68.6	69.5	4.85	4.72	4.79	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
1/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	15:00		Middle	2	29.40	29.40	29.4	8.22	8.22	8.2	28.88	28.88	28.9	75.2	73.8	74.5	4.88	4.78	4.83	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
3/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	15:18		Middle	2	28.00	28.00	28.0	8.03	8.04	8.0	28.34	28.34	28.3	75.0	75.5	75.3	4.66	5.03	4.85	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
5/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	15:58		Middle	2	26.90	26.90	26.9	8.17	8.17	8.2	28.43	28.43	28.4	82.7	80.6	81.7	5.60	5.44	5.52	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	17:40		Middle	2	27.30	27.30	27.3	8.28	8.28	8.3	29.05	29.05	29.1	62.9	64.7	63.8	4.24	4.35	4.30	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
10/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	10:30		Middle	1	28.70	28.70	28.7	8.30	8.30	8.3	28.15	28.15	28.2	66.9	67.1	67.0	4.52	4.53	4.53	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
12/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:35		Middle	2	27.10	27.10	27.1	8.17	8.17	8.2	30.02	30.02	30.0	66.9	68.9	67.9	4.47	4.60	4.54	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	13:52		Middle	1	26.40	26.40	26.4	8.15	8.15	8.2	28.65	28.65	28.7	58.7	57.5	58.1	4.02	3.94	3.98	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
17/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:30		Middle	1	26.70	26.70	26.7	8.10	8.10	8.1	29.56	29.56	29.6	67.0	68.0	67.5	4.54	4.61	4.58	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
19/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	15:03		Middle	2	27.60	27.60	27.6	8.01	8.01	8.0	28.09	28.09	28.1	50.0	49.6	49.8	3.36	3.34	3.35	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21/8/2015	-	Fine	Surface	1	27.50	27.50	27.5	8.18	8.18	8.2	24.57	24.57	24.6	45.1	44.3	44.7	3.10	3.04	3.07	
	14:55		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Bottom	3	26.80	26.80	26.8	8.06	8.06	8.1	29.76	29.76	29.8	74.2	72.2	73.2	5.01	4.88	4.95	
25/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:56		Middle	2	27.00	27.00	27.0	8.19	8.19	8.2	29.73	29.73	29.7	74.1	71.9	73.0	4.99	4.83	4.91	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
27/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:05		Middle	2	27.20	27.20	27.2	8.09	8.09	8.1	28.63	28.63	28.6	57.5	56.7	57.1	3.88	3.82	3.85	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.



**Water Monitoring Result at Ex-WPCWA SW - South-western corners of ex-Public Cargo Works Area  
Mid-Ebb Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature			pH			Salinity			DO Saturation			DO		
					°C			-			ppt			%			mg/L		
					Value	Average		Value	Average		Value	Average		Value	Average		Value	Average	
28/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	8:47		Middle	1.5	27.20	27.20	27.2	8.06	8.06	8.1	25.02	25.02	25.0	61.5	61.3	61.4	4.23	4.22	4.23
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
30/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:26		Middle	1.5	26.50	26.50	26.5	8.26	8.26	8.3	24.96	24.96	25.0	57.6	56.9	57.3	4.02	3.97	4.00
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
1/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:27		Middle	1.5	25.70	25.70	25.7	8.19	8.19	8.2	29.79	29.79	29.8	51.1	49.9	50.5	3.52	3.44	3.48
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
3/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	15:01		Middle	1.5	26.50	26.50	26.5	8.16	8.16	8.2	20.93	20.93	20.9	26.1	26.0	26.1	1.85	1.85	<u>1.85</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
5/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	15:41		Middle	1.0	26.40	26.40	26.4	8.29	8.29	8.3	27.42	27.42	27.4	40.2	40.3	40.3	2.77	2.78	<u>2.78</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
7/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	17:21		Middle	1.0	27.70	27.70	27.7	8.45	8.44	8.4	20.00	20.00	20.0	48.1	47.4	47.8	3.38	3.33	3.36
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
10/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	10:14		Middle	1.5	26.70	26.70	26.7	8.40	8.40	8.4	22.90	22.90	22.9	61.2	60.6	60.9	4.31	4.27	4.29
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
12/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:24		Middle	1.0	26.70	26.70	26.7	8.27	8.27	8.3	25.18	25.18	25.2	50.9	50.4	50.7	3.53	3.50	3.52
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	11:37		Middle	1.0	26.20	26.20	26.2	8.35	8.35	8.4	20.15	20.15	20.2	56.4	56.8	56.6	4.07	4.10	4.09
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
17/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	16:02		Middle	1.0	26.70	26.70	26.7	8.02	8.02	8.0	26.86	26.86	26.9	38.1	37.5	37.8	2.61	2.57	<u>2.59</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
19/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	14:50		Middle	1.0	26.80	26.80	26.8	8.11	8.11	8.1	24.28	24.28	24.3	40.8	41.3	41.1	2.84	2.89	<u>2.87</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	14:41		Middle	1.5	25.80	25.80	25.8	8.20	8.20	8.2	31.10	31.11	31.1	58.2	58.6	58.4	3.96	3.99	3.98
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
25/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:42		Middle	1.0	26.30	26.30	26.3	8.27	8.27	8.3	30.02	30.02	30.0	59.0	59.9	59.5	4.01	4.07	4.04
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
27/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
	9:54		Middle	1.0	25.90	25.90	25.9	8.10	8.10	8.1	27.93	27.93	27.9	40.7	40.8	40.8	2.82	2.83	<u>2.83</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.





**Water Monitoring Result at Ex-WPCWA SE - South-eastern corners of ex-Public Cargo Works Area  
Mid-Ebb Tide**

Date	Time	Weater Condition	Sampling Depth		Water Temperature			pH			Salinity		DO Saturation		DO				
					°C			-			ppt		%		mg/L				
					Value	Average		Value	Average		Value	Average	Value	Average	Value	Average			
28/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
30/7/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
1/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
3/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
5/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
7/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Middle	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
10/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	10:12		Middle	1.0	26.60	26.60	26.6	8.39	8.39	8.4	28.87	28.87	28.9	71.7	69.8	70.8	4.89	4.76	4.83
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
12/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	11:20		Middle	0.5	26.90	26.90	26.9	8.26	8.26	8.3	30.92	30.92	30.9	61.5	60.3	60.9	4.12	4.04	4.08
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
14/8/2015	-	Cloudy	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	11:35		Middle	1.0	26.00	26.00	26.0	8.26	8.26	8.3	28.93	28.93	28.9	50.7	52.2	51.5	3.49	3.59	<u>3.54</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
17/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	15:58		Middle	0.5	27.30	27.30	27.3	8.10	8.10	8.1	28.19	28.19	28.2	37.0	37.3	37.2	2.49	2.52	<u>2.51</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
19/8/2015	-	Sunny	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	14:46		Middle	0.5	27.30	27.30	27.3	8.19	8.19	8.2	30.48	30.48	30.5	50.0	48.9	49.5	3.34	3.26	<u>3.30</u>
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
21/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	14:35		Middle	1.0	26.50	26.50	26.5	8.16	8.16	8.2	31.04	31.04	31.0	59.4	58.4	58.9	4.00	3.93	3.97
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
25/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	9:40		Middle	0.5	26.50	26.50	26.5	8.24	8.24	8.2	31.36	31.36	31.4	70.9	68.6	69.8	4.76	4.60	4.68
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
27/8/2015	-	Fine	Surface	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
	9:48		Middle	0.5	26.00	26.00	26.0	8.20	8.20	8.2	32.61	32.61	32.6	63.6	62.2	62.9	4.29	4.20	4.25
	-		Bottom	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-

Remarks:  
Single underline denotes exceedance over Action Level.  
Double underline denotes exceedance over Limit Level.





### Graphic Presentation of Enhanced Water Monitoring Results (DO) at C6 - Excelsior Hotel

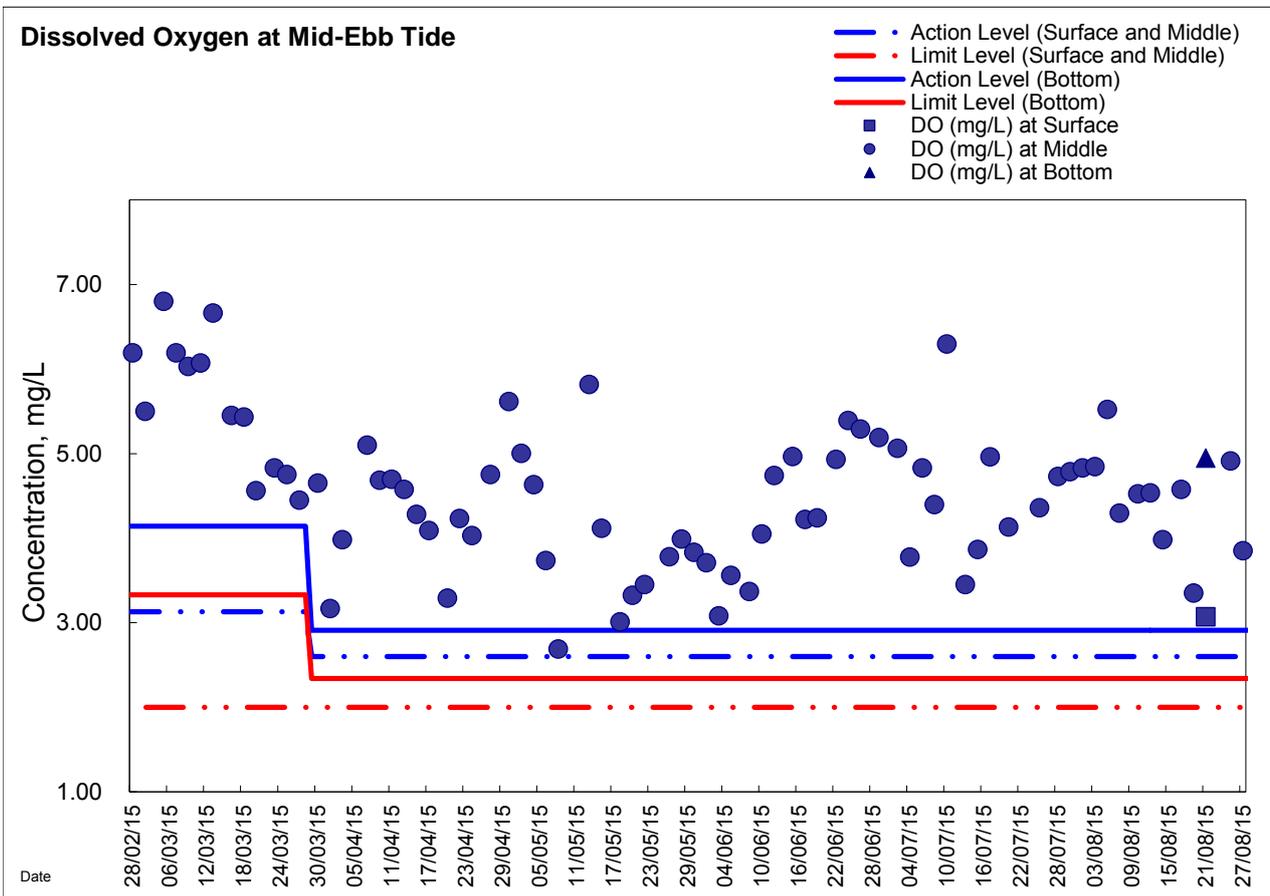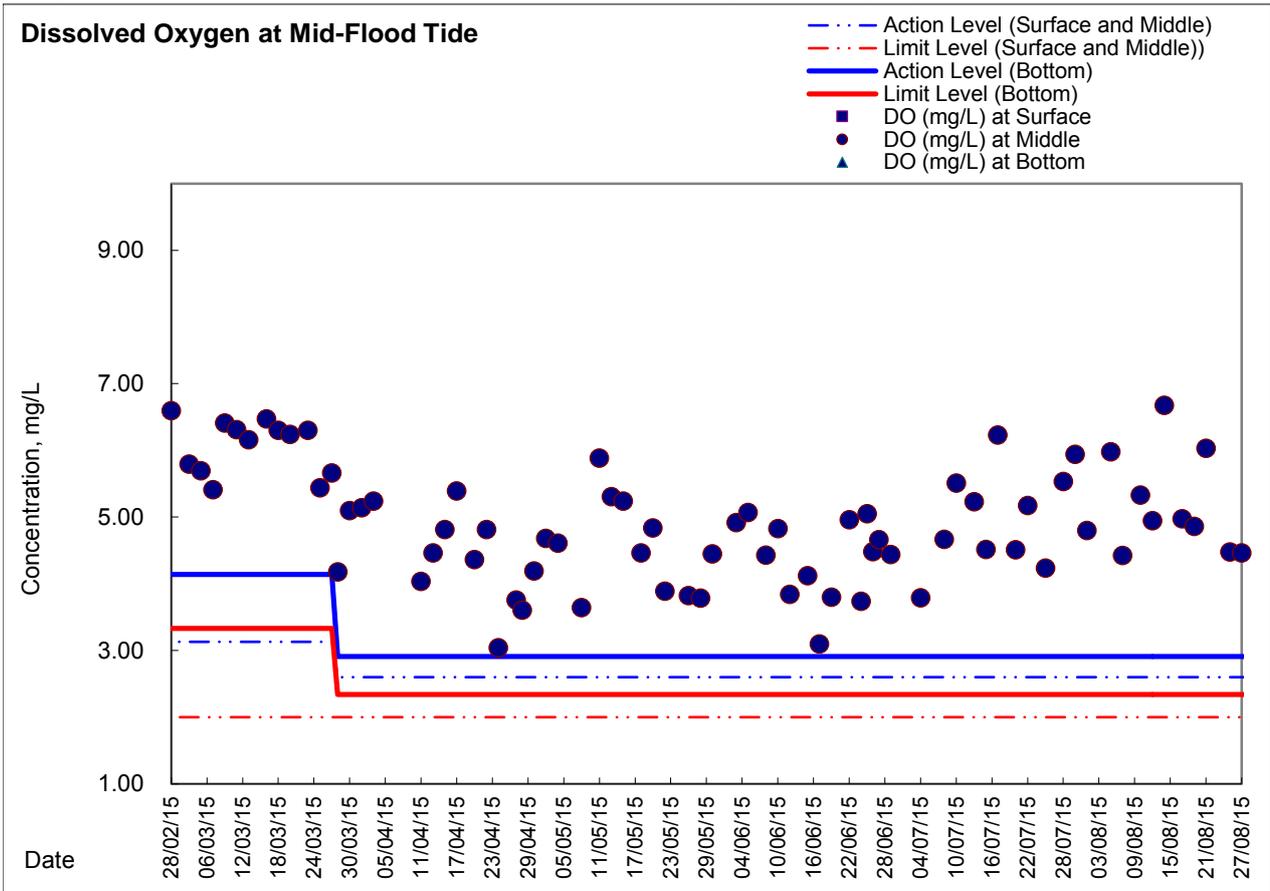





### Graphic Presentation of Enhanced Water Monitoring Results (DO) at Ex-WPCWA SW - South-western corners of ex-Public Cargo Works Area

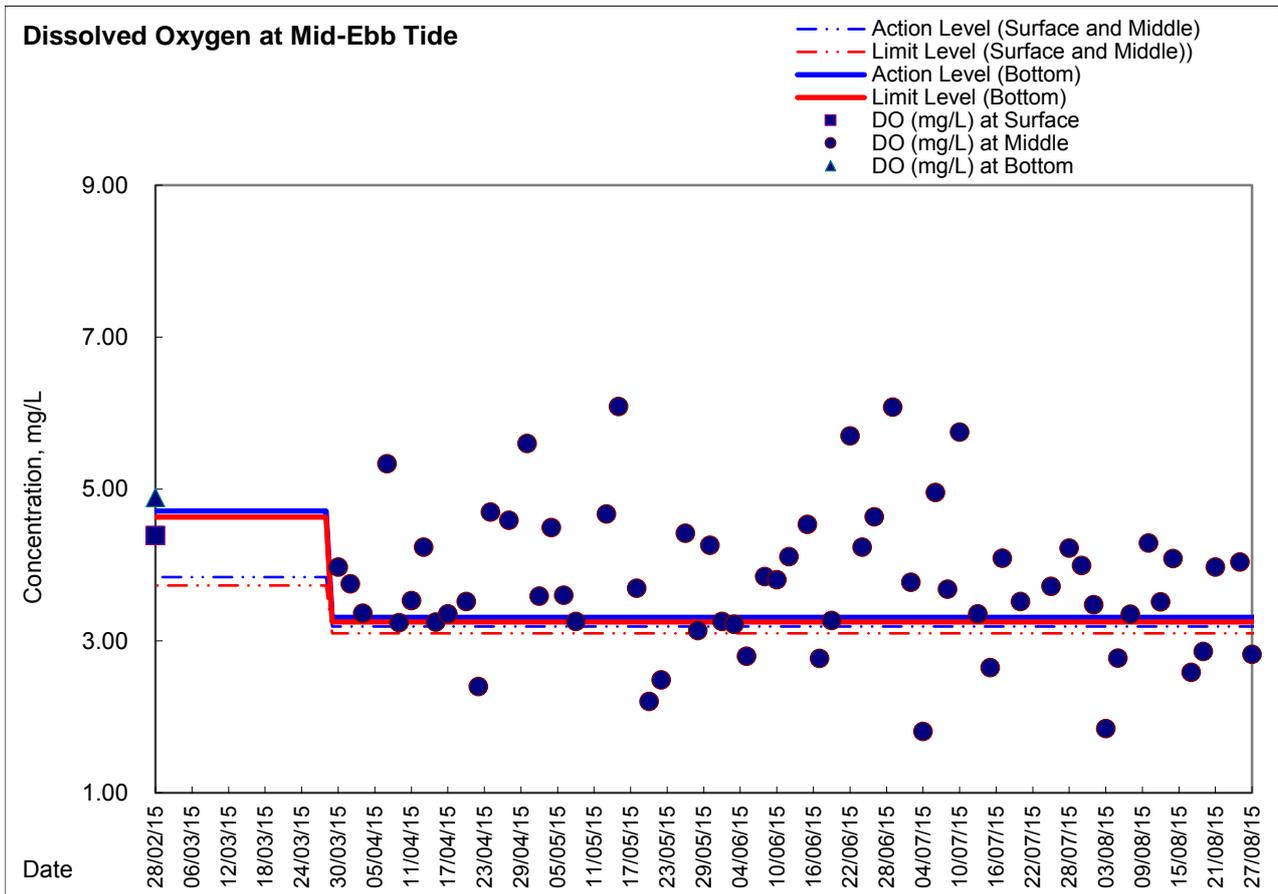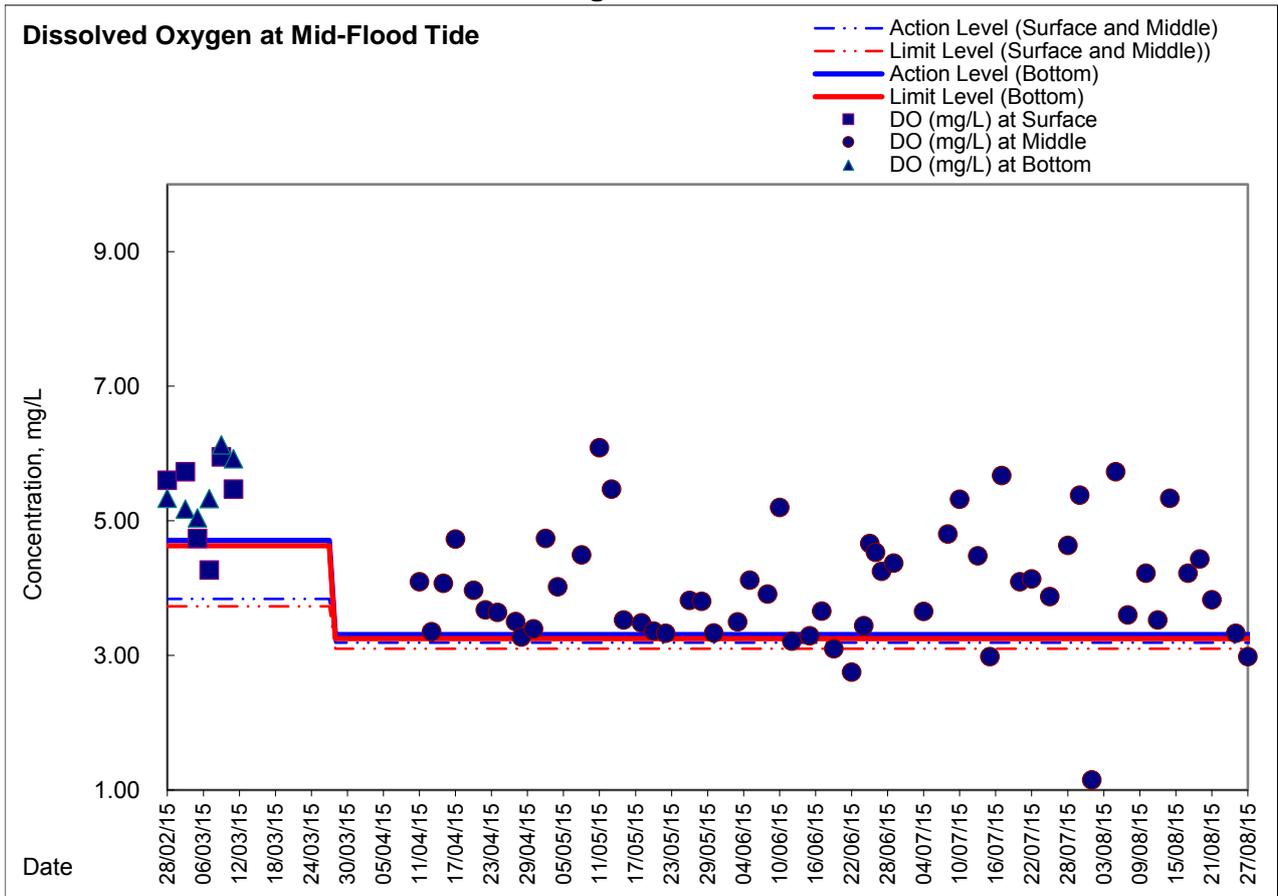



### Graphic Presentation of Enhanced Water Monitoring Results (DO) at Ex-WPCWA SE - South-eastern corners of ex-Public Cargo Works Area

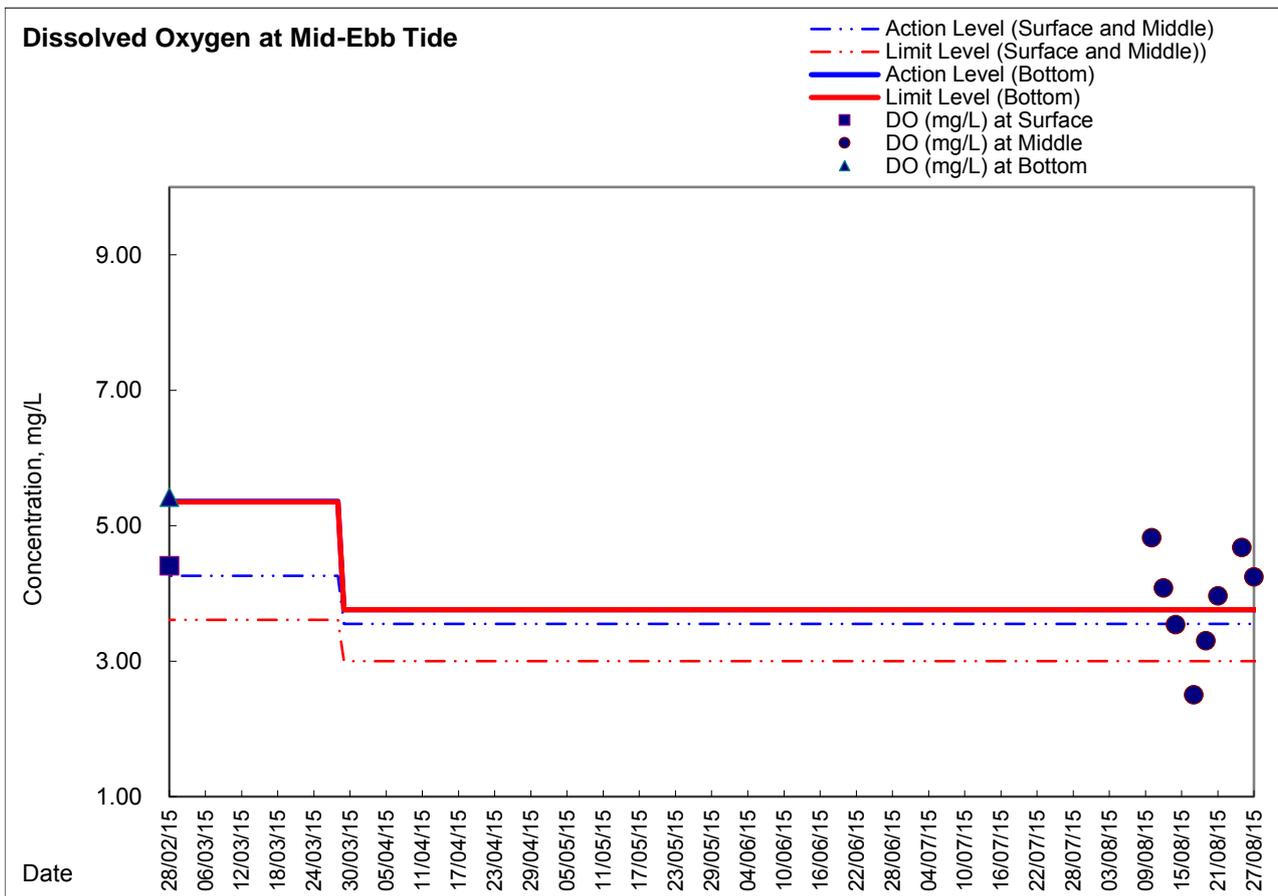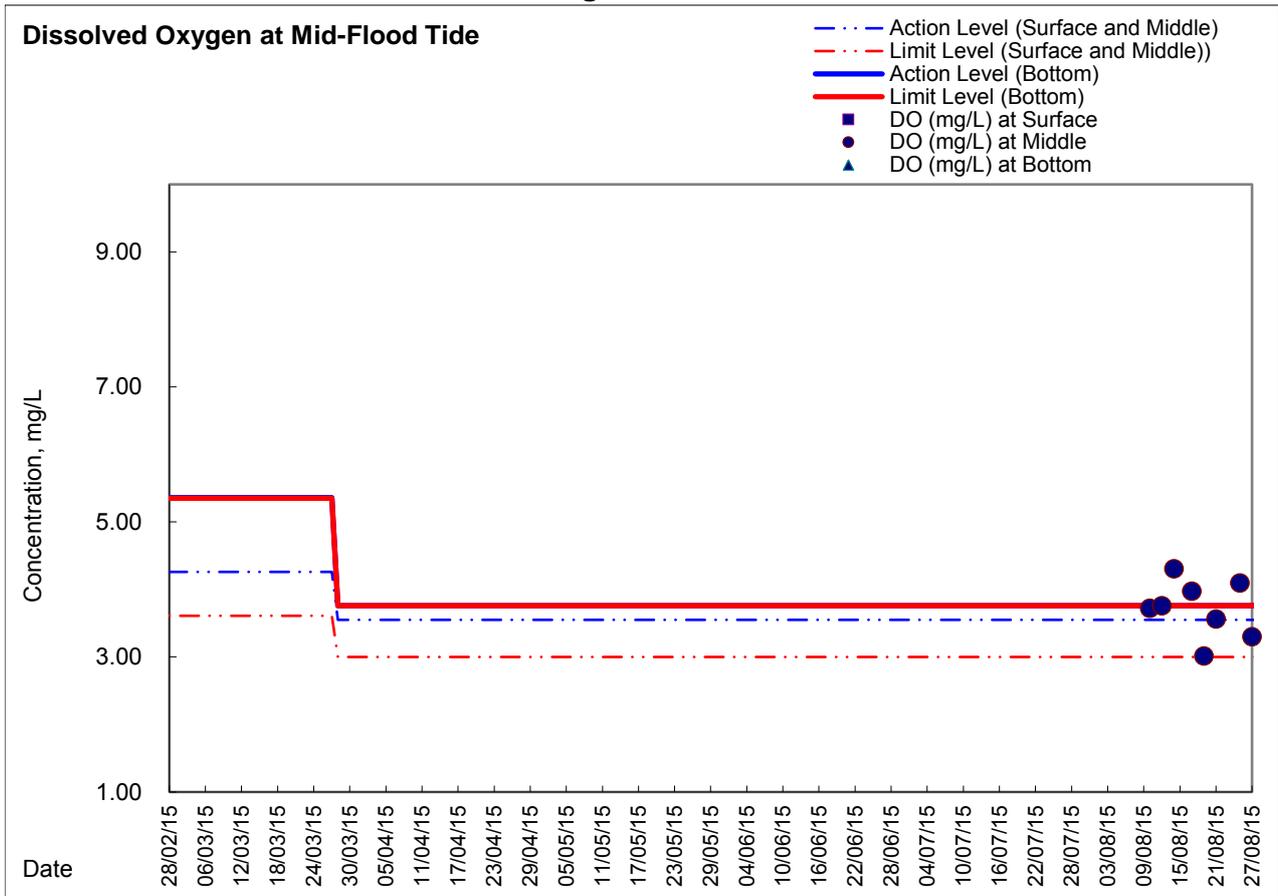



***Appendix 5.5***

***Real-time Noise Monitoring Results and Graphical Presentations***

Real-time Noise Data	RTN2a (Hong Kong Electric Centre)				
Normal Day 07:00-19:00	1/8/2015 12:01 64	6/8/2015 18:31 64	12/8/2015 13:01 61	18/8/2015 7:31 63	22/8/2015 14:01 64
	1/8/2015 12:31 64	7/8/2015 7:01 62	12/8/2015 13:31 61	18/8/2015 8:01 63	22/8/2015 14:31 66
	1/8/2015 13:01 67	7/8/2015 7:31 63	12/8/2015 14:01 51	18/8/2015 8:31 64	22/8/2015 15:01 66
28/7/2015 7:01 62	1/8/2015 13:31 60	7/8/2015 8:01 63	12/8/2015 14:31 65	18/8/2015 9:01 64	22/8/2015 15:31 65
28/7/2015 7:31 63	1/8/2015 14:01 65	7/8/2015 8:31 65	12/8/2015 15:01 65	18/8/2015 9:31 65	22/8/2015 16:01 67
28/7/2015 8:01 65	1/8/2015 14:31 64	7/8/2015 9:01 66	12/8/2015 15:31 64	18/8/2015 10:01 65	22/8/2015 16:31 64
28/7/2015 8:31 62	1/8/2015 15:01 66	7/8/2015 9:31 67	12/8/2015 16:01 57	18/8/2015 10:31 65	22/8/2015 17:01 63
28/7/2015 9:01 61	1/8/2015 15:31 65	7/8/2015 10:01 66	12/8/2015 16:31 66	18/8/2015 11:01 66	22/8/2015 17:31 63
28/7/2015 9:31 54	1/8/2015 16:01 66	7/8/2015 10:31 66	12/8/2015 17:01 65	18/8/2015 11:31 65	22/8/2015 18:01 63
28/7/2015 10:01 60	1/8/2015 16:31 67	7/8/2015 11:01 66	12/8/2015 17:31 65	18/8/2015 12:01 64	22/8/2015 18:31 63
28/7/2015 10:31 60	1/8/2015 17:01 65	7/8/2015 11:31 65	12/8/2015 18:01 65	18/8/2015 12:31 64	24/8/2015 7:01 62
28/7/2015 11:01 62	1/8/2015 17:31 65	7/8/2015 12:01 64	12/8/2015 18:31 65	18/8/2015 13:01 65	24/8/2015 7:31 62
28/7/2015 11:31 55	1/8/2015 18:01 64	7/8/2015 12:31 64	13/8/2015 7:01 62	18/8/2015 13:31 66	24/8/2015 8:01 63
28/7/2015 12:01 63	1/8/2015 18:31 63	7/8/2015 13:01 66	13/8/2015 7:31 62	18/8/2015 14:01 66	24/8/2015 8:31 64
28/7/2015 12:31 64	3/8/2015 7:01 63	7/8/2015 13:31 67	13/8/2015 8:01 63	18/8/2015 14:31 65	24/8/2015 9:01 65
28/7/2015 13:01 59	3/8/2015 7:31 63	7/8/2015 14:01 66	13/8/2015 8:31 64	18/8/2015 15:01 65	24/8/2015 9:31 65
28/7/2015 13:31 63	3/8/2015 8:01 63	7/8/2015 14:31 67	13/8/2015 9:01 65	18/8/2015 15:31 65	24/8/2015 10:01 66
28/7/2015 14:01 61	3/8/2015 8:31 66	7/8/2015 15:01 67	13/8/2015 9:31 67	18/8/2015 16:01 66	24/8/2015 10:31 66
28/7/2015 14:31 62	3/8/2015 9:01 66	7/8/2015 15:31 73	13/8/2015 10:01 65	18/8/2015 16:31 66	24/8/2015 11:01 63
28/7/2015 15:01 60	3/8/2015 9:31 66	7/8/2015 16:01 73	13/8/2015 10:31 66	18/8/2015 17:01 58	24/8/2015 11:31 63
28/7/2015 15:31 67	3/8/2015 10:01 56	7/8/2015 16:31 65	13/8/2015 11:01 44	18/8/2015 17:31 65	24/8/2015 12:01 63
28/7/2015 16:01 61	3/8/2015 10:31 60	7/8/2015 17:01 64	13/8/2015 11:31 65	18/8/2015 18:01 63	24/8/2015 12:31 63
28/7/2015 16:31 62	3/8/2015 11:01 67	7/8/2015 17:31 71	13/8/2015 12:01 63	18/8/2015 18:31 63	24/8/2015 13:01 65
28/7/2015 17:01 56	3/8/2015 11:31 66	7/8/2015 18:01 61	13/8/2015 12:31 63	19/8/2015 7:01 62	24/8/2015 13:31 67
28/7/2015 17:31 67	3/8/2015 12:01 63	7/8/2015 18:31 64	13/8/2015 13:01 66	19/8/2015 7:31 63	24/8/2015 14:01 66
28/7/2015 18:01 66	3/8/2015 12:31 64	8/8/2015 7:01 61	13/8/2015 13:31 66	19/8/2015 8:01 63	24/8/2015 14:31 65
28/7/2015 18:31 65	3/8/2015 13:01 67	8/8/2015 7:31 62	13/8/2015 14:01 66	19/8/2015 8:31 64	24/8/2015 15:01 67
29/7/2015 7:01 63	3/8/2015 13:31 60	8/8/2015 8:01 64	13/8/2015 14:31 65	19/8/2015 9:01 64	24/8/2015 15:31 66
29/7/2015 7:31 63	3/8/2015 14:01 59	8/8/2015 8:31 65	13/8/2015 15:01 66	19/8/2015 9:31 65	24/8/2015 16:01 66
29/7/2015 8:01 64	3/8/2015 14:31 62	8/8/2015 9:01 65	13/8/2015 15:31 66	19/8/2015 10:01 65	24/8/2015 16:31 57
29/7/2015 8:31 51	3/8/2015 15:01 63	8/8/2015 9:31 65	13/8/2015 16:01 66	19/8/2015 10:31 65	24/8/2015 17:01 62
29/7/2015 9:01 62	3/8/2015 15:31 66	8/8/2015 10:01 65	13/8/2015 16:31 66	19/8/2015 11:01 66	24/8/2015 17:31 65
29/7/2015 9:31 68	3/8/2015 16:01 39	8/8/2015 10:31 66	13/8/2015 17:01 51	19/8/2015 11:31 66	24/8/2015 18:01 63
29/7/2015 10:01 67	3/8/2015 16:31 65	8/8/2015 11:01 51	13/8/2015 17:31 64	19/8/2015 12:01 62	24/8/2015 18:31 63
29/7/2015 10:31 50	3/8/2015 17:01 66	8/8/2015 11:31 65	13/8/2015 18:01 64	19/8/2015 12:31 63	25/8/2015 7:01 62
29/7/2015 11:01 66	3/8/2015 17:31 65	8/8/2015 12:01 63	13/8/2015 18:31 64	19/8/2015 13:01 66	25/8/2015 7:31 62
29/7/2015 11:31 66	3/8/2015 18:01 64	8/8/2015 12:31 64	14/8/2015 7:01 63	19/8/2015 13:31 66	25/8/2015 8:01 63
29/7/2015 12:01 63	3/8/2015 18:31 63	8/8/2015 13:01 66	14/8/2015 7:31 65	19/8/2015 14:01 67	25/8/2015 8:31 66
29/7/2015 12:31 64	4/8/2015 7:01 62	8/8/2015 13:31 53	14/8/2015 8:01 64	19/8/2015 14:31 64	25/8/2015 9:01 66
29/7/2015 13:01 62	4/8/2015 7:31 63	8/8/2015 14:01 66	14/8/2015 8:31 70	19/8/2015 15:01 64	25/8/2015 9:31 65
29/7/2015 13:31 67	4/8/2015 8:01 65	8/8/2015 14:31 65	14/8/2015 9:01 68	19/8/2015 15:31 64	25/8/2015 10:01 66
29/7/2015 14:01 65	4/8/2015 8:31 57	8/8/2015 15:01 66	14/8/2015 9:31 67	19/8/2015 16:01 66	25/8/2015 10:31 46
29/7/2015 14:31 63	4/8/2015 9:01 67	8/8/2015 15:31 65	14/8/2015 10:01 68	19/8/2015 16:31 65	25/8/2015 11:01 71
29/7/2015 15:01 52	4/8/2015 9:31 66	8/8/2015 16:01 65	14/8/2015 10:31 66	19/8/2015 17:01 64	25/8/2015 11:31 64
29/7/2015 15:31 55	4/8/2015 10:01 67	8/8/2015 16:31 64	14/8/2015 11:01 42	19/8/2015 17:31 63	25/8/2015 12:01 65
29/7/2015 16:01 59	4/8/2015 10:31 67	8/8/2015 17:01 64	14/8/2015 11:31 64	19/8/2015 18:01 62	25/8/2015 12:31 64
29/7/2015 16:31 59	4/8/2015 11:01 67	8/8/2015 17:31 63	14/8/2015 12:01 63	19/8/2015 18:31 61	25/8/2015 13:01 67
29/7/2015 17:01 67	4/8/2015 11:31 65	8/8/2015 18:01 63	14/8/2015 12:31 62	20/8/2015 7:01 62	25/8/2015 13:31 59
29/7/2015 17:31 66	4/8/2015 12:01 64	8/8/2015 18:31 64	14/8/2015 13:01 64	20/8/2015 7:31 63	25/8/2015 14:01 67
29/7/2015 18:01 66	4/8/2015 12:31 63	10/8/2015 7:01 63	14/8/2015 13:31 65	20/8/2015 8:01 63	25/8/2015 14:31 66
29/7/2015 18:31 65	4/8/2015 13:01 65	10/8/2015 7:31 64	14/8/2015 14:01 64	20/8/2015 8:31 65	25/8/2015 15:01 61
30/7/2015 7:01 63	4/8/2015 13:31 66	10/8/2015 8:01 63	14/8/2015 14:31 65	20/8/2015 9:01 65	25/8/2015 15:31 59
30/7/2015 7:31 63	4/8/2015 14:01 66	10/8/2015 8:31 64	14/8/2015 15:01 64	20/8/2015 9:31 65	25/8/2015 16:01 55
30/7/2015 8:01 64	4/8/2015 14:31 65	10/8/2015 9:01 65	14/8/2015 15:31 64	20/8/2015 10:01 65	25/8/2015 16:31 67
30/7/2015 8:31 66	4/8/2015 15:01 64	10/8/2015 9:31 66	14/8/2015 16:01 65	20/8/2015 10:31 65	25/8/2015 17:01 64
30/7/2015 9:01 67	4/8/2015 15:31 64	10/8/2015 10:01 65	14/8/2015 16:31 64	20/8/2015 11:01 64	25/8/2015 17:31 63
30/7/2015 9:31 66	4/8/2015 16:01 65	10/8/2015 10:31 66	14/8/2015 17:01 65	20/8/2015 11:31 57	25/8/2015 18:01 63
30/7/2015 10:01 66	4/8/2015 16:31 65	10/8/2015 11:01 66	14/8/2015 17:31 65	20/8/2015 12:01 64	25/8/2015 18:31 62
30/7/2015 10:31 66	4/8/2015 17:01 65	10/8/2015 11:31 64	14/8/2015 18:01 64	20/8/2015 12:31 64	26/8/2015 7:01 62
30/7/2015 11:01 66	4/8/2015 17:31 64	10/8/2015 12:01 63	14/8/2015 18:31 62	20/8/2015 13:01 65	26/8/2015 7:31 61
30/7/2015 11:31 65	4/8/2015 18:01 63	10/8/2015 12:31 64	15/8/2015 7:01 64	20/8/2015 13:31 66	26/8/2015 8:01 62
30/7/2015 12:01 64	4/8/2015 18:31 63	10/8/2015 13:01 66	15/8/2015 7:31 63	20/8/2015 14:01 66	26/8/2015 8:31 63
30/7/2015 12:31 64	5/8/2015 7:01 62	10/8/2015 13:31 66	15/8/2015 8:01 65	20/8/2015 14:31 65	26/8/2015 9:01 66
30/7/2015 13:01 66	5/8/2015 7:31 63	10/8/2015 14:01 65	15/8/2015 8:31 65	20/8/2015 15:01 65	26/8/2015 9:31 63
30/7/2015 13:31 67	5/8/2015 8:01 63	10/8/2015 14:31 65	15/8/2015 9:01 65	20/8/2015 15:31 65	26/8/2015 10:01 65
30/7/2015 14:01 66	5/8/2015 8:31 65	10/8/2015 15:01 64	15/8/2015 9:31 64	20/8/2015 16:01 65	26/8/2015 10:31 64
30/7/2015 14:31 66	5/8/2015 9:01 66	10/8/2015 15:31 64	15/8/2015 10:01 66	20/8/2015 16:31 65	26/8/2015 11:01 65
30/7/2015 15:01 66	5/8/2015 9:31 66	10/8/2015 16:01 66	15/8/2015 10:31 65	20/8/2015 17:01 65	26/8/2015 11:31 64
30/7/2015 15:31 66	5/8/2015 10:01 66	10/8/2015 16:31 67	15/8/2015 11:01 65	20/8/2015 17:31 62	26/8/2015 12:01 63
30/7/2015 16:01 65	5/8/2015 10:31 66	10/8/2015 17:01 66	15/8/2015 11:31 66	20/8/2015 18:01 63	26/8/2015 12:31 62
30/7/2015 16:31 66	5/8/2015 11:01 43	10/8/2015 17:31 66	15/8/2015 12:01 64	20/8/2015 18:31 62	26/8/2015 13:01 57
30/7/2015 17:01 66	5/8/2015 11:31 65	10/8/2015 18:01 64	15/8/2015 12:31 63	21/8/2015 7:01 63	26/8/2015 13:31 62
30/7/2015 17:31 65	5/8/2015 12:01 63	10/8/2015 18:31 63	15/8/2015 13:01 64	21/8/2015 7:31 63	26/8/2015 14:01 59
30/7/2015 18:01 64	5/8/2015 12:31 63	11/8/2015 7:01 63	15/8/2015 13:31 65	21/8/2015 8:01 63	26/8/2015 14:31 64
30/7/2015 18:31 64	5/8/2015 13:01 65	11/8/2015 7:31 63	15/8/2015 14:01 65	21/8/2015 8:31 65	26/8/2015 15:01 67
31/7/2015 7:01 62	5/8/2015 13:31 67	11/8/2015 8:01 62	15/8/2015 14:31 64	21/8/2015 9:01 65	26/8/2015 15:31 59
31/7/2015 7:31 63	5/8/2015 14:01 67	11/8/2015 8:31 65	15/8/2015 15:01 64	21/8/2015 9:31 65	26/8/2015 16:01 64
31/7/2015 8:01 64	5/8/2015 14:31 67	11/8/2015 9:01 66	15/8/2015 15:31 65	21/8/2015 10:01 65	26/8/2015 16:31 67
31/7/2015 8:31 66	5/8/2015 15:01 66	11/8/2015 9:31 66	15/8/2015 16:01 65	21/8/2015 10:31 64	26/8/2015 17:01 65
31/7/2015 9:01 67	5/8/2015 15:31 59	11/8/2015 10:01 66	15/8/2015 16:31 65	21/8/2015 11:01 65	26/8/2015 17:31 66
31/7/2015 9:31 60	5/8/2015 16:01 67	11/8/2015 10:31 61	15/8/2015 17:01 64	21/8/2015 11:31 64	26/8/2015 18:01 64
31/7/2015 10:01 66	5/8/2015 16:31 67	11/8/2015 11:01 67	15/8/2015 17:31 62	21/8/2015 12:01 64	26/8/2015 18:31 64
31/7/2015 10:31 66	5/8/2015 17:01 67	11/8/2015 11:31 65	15/8/2015 18:01 63	21/8/2015 12:31 63	27/8/2015 7:01 62
31/7/2015 11:01 66	5/8/2015 17:31 64	11/8/2015 12:01 63</			

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
		30/7/2015 19:36	55	1/8/2015 20:41	42	2/8/2015 13:46	56	2/8/2015 22:51	62	5/8/2015 19:56	53
		30/7/2015 19:41	57	1/8/2015 20:46	54	2/8/2015 13:51	54	2/8/2015 22:56	61	5/8/2015 20:01	51
		30/7/2015 19:46	58	1/8/2015 20:51	62	2/8/2015 13:56	54	3/8/2015 19:01	57	5/8/2015 20:06	54
	<u>Normal Day 19:00-23:00.</u>	30/7/2015 19:51	54	1/8/2015 20:56	54	2/8/2015 14:01	56	3/8/2015 19:06	57	5/8/2015 20:11	45
	<u>Sunday &amp; Holiday</u>	30/7/2015 19:56	58	1/8/2015 21:01	49	2/8/2015 14:06	53	3/8/2015 19:11	58	5/8/2015 20:16	54
	<u>07:00-23:00</u>	30/7/2015 20:01	62	1/8/2015 21:06	44	2/8/2015 14:11	56	3/8/2015 19:16	56	5/8/2015 20:21	49
28/7/2015 19:01	62	30/7/2015 20:06	50	1/8/2015 21:11	62	2/8/2015 14:16	56	3/8/2015 19:21	51	5/8/2015 20:26	53
28/7/2015 19:06	62	30/7/2015 20:11	49	1/8/2015 21:16	62	2/8/2015 14:21	55	3/8/2015 19:26	58	5/8/2015 20:31	50
28/7/2015 19:11	63	30/7/2015 20:16	52	1/8/2015 21:21	59	2/8/2015 14:26	53	3/8/2015 19:31	53	5/8/2015 20:36	48
28/7/2015 19:16	63	30/7/2015 20:21	55	1/8/2015 21:26	62	2/8/2015 14:31	53	3/8/2015 19:36	52	5/8/2015 20:41	54
28/7/2015 19:21	62	30/7/2015 20:26	57	1/8/2015 21:31	62	2/8/2015 14:36	55	3/8/2015 19:41	56	5/8/2015 20:46	52
28/7/2015 19:26	62	30/7/2015 20:31	55	1/8/2015 21:36	61	2/8/2015 14:41	48	3/8/2015 19:46	54	5/8/2015 20:51	62
28/7/2015 19:31	61	30/7/2015 20:36	50	1/8/2015 21:41	62	2/8/2015 14:46	55	3/8/2015 19:51	56	5/8/2015 20:56	46
28/7/2015 19:36	62	30/7/2015 20:41	46	1/8/2015 21:46	62	2/8/2015 14:51	57	3/8/2015 19:56	53	5/8/2015 21:01	43
28/7/2015 19:41	62	30/7/2015 20:46	62	1/8/2015 21:51	62	2/8/2015 14:56	55	3/8/2015 20:01	56	5/8/2015 21:06	56
28/7/2015 19:46	61	30/7/2015 20:51	50	1/8/2015 21:56	50	2/8/2015 15:01	54	3/8/2015 20:06	54	5/8/2015 21:11	52
28/7/2015 19:51	61	30/7/2015 20:56	54	1/8/2015 22:01	61	2/8/2015 15:06	52	3/8/2015 20:11	51	5/8/2015 21:16	49
28/7/2015 19:56	62	30/7/2015 21:01	53	1/8/2015 22:06	62	2/8/2015 15:11	52	3/8/2015 20:16	53	5/8/2015 21:21	55
28/7/2015 20:01	61	30/7/2015 21:06	62	1/8/2015 22:11	62	2/8/2015 15:16	36	3/8/2015 20:21	48	5/8/2015 21:26	61
28/7/2015 20:06	63	30/7/2015 21:11	61	1/8/2015 22:16	61	2/8/2015 15:21	54	3/8/2015 20:26	62	5/8/2015 21:31	61
28/7/2015 20:11	62	30/7/2015 21:16	49	1/8/2015 22:21	61	2/8/2015 15:26	54	3/8/2015 20:31	61	5/8/2015 21:36	62
28/7/2015 20:16	63	30/7/2015 21:21	62	1/8/2015 22:26	61	2/8/2015 15:31	56	3/8/2015 20:36	62	5/8/2015 21:41	55
28/7/2015 20:21	59	30/7/2015 21:26	50	1/8/2015 22:31	57	2/8/2015 15:36	43	3/8/2015 20:41	52	5/8/2015 21:46	62
28/7/2015 20:26	53	30/7/2015 21:31	52	1/8/2015 22:36	61	2/8/2015 15:41	52	3/8/2015 20:46	62	5/8/2015 21:51	53
28/7/2015 20:31	53	30/7/2015 21:36	53	1/8/2015 22:41	61	2/8/2015 15:46	47	3/8/2015 20:51	56	5/8/2015 21:56	62
28/7/2015 20:36	51	30/7/2015 21:41	62	1/8/2015 22:46	61	2/8/2015 15:51	57	3/8/2015 20:56	50	5/8/2015 22:01	51
28/7/2015 20:41	54	30/7/2015 21:46	43	1/8/2015 22:51	62	2/8/2015 15:56	49	3/8/2015 21:01	62	5/8/2015 22:06	46
28/7/2015 20:46	54	30/7/2015 21:51	58	1/8/2015 22:56	62	2/8/2015 16:01	57	3/8/2015 21:06	62	5/8/2015 22:11	62
28/7/2015 20:51	62	30/7/2015 21:56	62	2/8/2015 7:01	60	2/8/2015 16:06	52	3/8/2015 21:11	53	5/8/2015 22:16	58
28/7/2015 20:56	57	30/7/2015 22:01	62	2/8/2015 7:06	60	2/8/2015 16:11	49	3/8/2015 21:16	62	5/8/2015 22:21	61
28/7/2015 21:01	62	30/7/2015 22:06	55	2/8/2015 7:11	60	2/8/2015 16:16	55	3/8/2015 21:21	52	5/8/2015 22:26	62
28/7/2015 21:06	49	30/7/2015 22:11	51	2/8/2015 7:16	61	2/8/2015 16:21	51	3/8/2015 21:26	52	5/8/2015 22:31	50
28/7/2015 21:11	57	30/7/2015 22:16	51	2/8/2015 7:21	62	2/8/2015 16:26	53	3/8/2015 21:31	62	5/8/2015 22:36	53
28/7/2015 21:16	45	30/7/2015 22:21	62	2/8/2015 7:26	61	2/8/2015 16:31	36	3/8/2015 21:36	61	5/8/2015 22:41	62
28/7/2015 21:21	62	30/7/2015 22:26	50	2/8/2015 7:31	61	2/8/2015 16:36	56	3/8/2015 21:41	62	5/8/2015 22:46	61
28/7/2015 21:26	62	30/7/2015 22:31	53	2/8/2015 7:36	60	2/8/2015 16:41	62	3/8/2015 21:46	56	5/8/2015 22:51	61
28/7/2015 21:31	49	30/7/2015 22:36	62	2/8/2015 7:41	61	2/8/2015 16:46	52	3/8/2015 21:51	61	5/8/2015 22:56	61
28/7/2015 21:36	55	30/7/2015 22:41	62	2/8/2015 7:46	61	2/8/2015 16:51	51	3/8/2015 21:56	62	6/8/2015 19:01	58
28/7/2015 21:41	54	30/7/2015 22:46	62	2/8/2015 7:51	62	2/8/2015 16:56	55	3/8/2015 22:01	49	6/8/2015 19:06	56
28/7/2015 21:46	54	30/7/2015 22:51	61	2/8/2015 7:56	61	2/8/2015 17:01	52	3/8/2015 22:06	62	6/8/2015 19:11	54
28/7/2015 21:51	56	30/7/2015 22:56	61	2/8/2015 8:01	62	2/8/2015 17:06	52	3/8/2015 22:11	61	6/8/2015 19:16	53
28/7/2015 21:56	51	31/7/2015 19:01	59	2/8/2015 8:06	61	2/8/2015 17:11	50	3/8/2015 22:16	52	6/8/2015 19:21	57
28/7/2015 22:01	61	31/7/2015 19:06	60	2/8/2015 8:11	51	2/8/2015 17:16	50	3/8/2015 22:21	62	6/8/2015 19:26	56
28/7/2015 22:06	62	31/7/2015 19:11	60	2/8/2015 8:16	62	2/8/2015 17:21	59	3/8/2015 22:26	52	6/8/2015 19:31	52
28/7/2015 22:11	52	31/7/2015 19:16	60	2/8/2015 8:21	61	2/8/2015 17:26	53	3/8/2015 22:31	62	6/8/2015 19:36	54
28/7/2015 22:16	52	31/7/2015 19:21	59	2/8/2015 8:26	61	2/8/2015 17:31	62	3/8/2015 22:36	40	6/8/2015 19:41	54
28/7/2015 22:21	55	31/7/2015 19:26	60	2/8/2015 8:31	53	2/8/2015 17:36	55	3/8/2015 22:41	62	6/8/2015 19:46	55
28/7/2015 22:26	62	31/7/2015 19:31	60	2/8/2015 8:36	56	2/8/2015 17:41	55	3/8/2015 22:46	61	6/8/2015 19:51	49
28/7/2015 22:31	55	31/7/2015 19:36	61	2/8/2015 8:41	58	2/8/2015 17:46	50	3/8/2015 22:51	62	6/8/2015 19:56	57
28/7/2015 22:36	55	31/7/2015 19:41	63	2/8/2015 8:46	52	2/8/2015 17:51	50	3/8/2015 22:56	61	6/8/2015 20:01	55
28/7/2015 22:41	62	31/7/2015 19:46	60	2/8/2015 8:51	52	2/8/2015 17:56	62	4/8/2015 19:01	56	6/8/2015 20:06	58
28/7/2015 22:46	47	31/7/2015 19:51	62	2/8/2015 8:56	56	2/8/2015 18:01	49	4/8/2015 19:06	57	6/8/2015 20:11	59
28/7/2015 22:51	61	31/7/2015 19:56	61	2/8/2015 9:01	56	2/8/2015 18:06	54	4/8/2015 19:11	54	6/8/2015 20:16	62
28/7/2015 22:56	62	31/7/2015 20:01	59	2/8/2015 9:06	54	2/8/2015 18:11	60	4/8/2015 19:16	59	6/8/2015 20:21	60
29/7/2015 19:01	63	31/7/2015 20:06	60	2/8/2015 9:11	57	2/8/2015 18:16	54	4/8/2015 19:21	55	6/8/2015 20:26	57
29/7/2015 19:06	62	31/7/2015 20:11	59	2/8/2015 9:16	56	2/8/2015 18:21	53	4/8/2015 19:26	56	6/8/2015 20:31	47
29/7/2015 19:11	63	31/7/2015 20:16	58	2/8/2015 9:21	55	2/8/2015 18:26	55	4/8/2015 19:31	50	6/8/2015 20:36	53
29/7/2015 19:16	62	31/7/2015 20:21	60	2/8/2015 9:26	53	2/8/2015 18:31	61	4/8/2015 19:36	56	6/8/2015 20:41	52
29/7/2015 19:21	63	31/7/2015 20:26	59	2/8/2015 9:31	53	2/8/2015 18:36	58	4/8/2015 19:41	59	6/8/2015 20:46	62
29/7/2015 19:26	61	31/7/2015 20:31	57	2/8/2015 9:36	54	2/8/2015 18:41	49	4/8/2015 19:46	52	6/8/2015 20:51	48
29/7/2015 19:31	63	31/7/2015 20:36	57	2/8/2015 9:41	55	2/8/2015 18:46	57	4/8/2015 19:51	55	6/8/2015 20:56	48
29/7/2015 19:36	62	31/7/2015 20:41	57	2/8/2015 9:46	58	2/8/2015 18:51	53	4/8/2015 19:56	56	6/8/2015 21:01	62
29/7/2015 19:41	62	31/7/2015 20:46	59	2/8/2015 9:51	64	2/8/2015 18:56	62	4/8/2015 20:01	51	6/8/2015 21:06	53
29/7/2015 19:46	61	31/7/2015 20:51	58	2/8/2015 9:56	54	2/8/2015 19:01	47	4/8/2015 20:06	58	6/8/2015 21:11	62
29/7/2015 19:51	60	31/7/2015 20:56	60	2/8/2015 10:01	49	2/8/2015 19:06	51	4/8/2015 20:11	60	6/8/2015 21:16	62
29/7/2015 19:56	62	31/7/2015 21:01	62	2/8/2015 10:06	54	2/8/2015 19:11	48	4/8/2015 20:16	59	6/8/2015 21:21	62
29/7/2015 20:01	62	31/7/2015 21:06	59	2/8/2015 10:11	51	2/8/2015 19:16	52	4/8/2015 20:21	58	6/8/2015 21:26	62
29/7/2015 20:06	62	31/7/2015 21:11	60	2/8/2015 10:16	56	2/8/2015 19:21	52	4/8/2015 20:26	59	6/8/2015 21:31	62
29/7/2015 20:11	64	31/7/2015 21:16	58	2/8/2015 10:21	54	2/8/2015 19:26	49	4/8/2015 20:31	59	6/8/2015 21:36	54
29/7/2015 20:16	60	31/7/2015 21:21	59	2/8/2015 10:26	57	2/8/2015 19:31	44	4/8/2015 20:36	57	6/8/2015 21:41	62

Real-time Noise Data	RTN2a (Hong Kong Electric Centre)										
7/8/2015 21:01	62	9/8/2015 10:06	61	9/8/2015 19:11	60	11/8/2015 20:16	56	13/8/2015 21:21	53	15/8/2015 22:26	51
7/8/2015 21:06	62	9/8/2015 10:11	61	9/8/2015 19:16	56	11/8/2015 20:21	49	13/8/2015 21:26	46	15/8/2015 22:31	50
7/8/2015 21:11	36	9/8/2015 10:16	61	9/8/2015 19:21	62	11/8/2015 20:26	44	13/8/2015 21:31	49	15/8/2015 22:36	39
7/8/2015 21:16	61	9/8/2015 10:21	61	9/8/2015 19:26	61	11/8/2015 20:31	46	13/8/2015 21:36	45	15/8/2015 22:41	45
7/8/2015 21:21	45	9/8/2015 10:26	61	9/8/2015 19:31	61	11/8/2015 20:36	62	13/8/2015 21:41	52	15/8/2015 22:46	55
7/8/2015 21:26	55	9/8/2015 10:31	61	9/8/2015 19:36	62	11/8/2015 20:41	62	13/8/2015 21:46	52	15/8/2015 22:51	62
7/8/2015 21:31	61	9/8/2015 10:36	58	9/8/2015 19:41	61	11/8/2015 20:46	62	13/8/2015 21:51	49	15/8/2015 22:56	53
7/8/2015 21:36	61	9/8/2015 10:41	61	9/8/2015 19:46	61	11/8/2015 20:51	53	13/8/2015 21:56	62	16/8/2015 7:01	59
7/8/2015 21:41	36	9/8/2015 10:46	61	9/8/2015 19:51	62	11/8/2015 20:56	62	13/8/2015 22:01	49	16/8/2015 7:06	61
7/8/2015 21:46	62	9/8/2015 10:51	61	9/8/2015 19:56	61	11/8/2015 21:01	51	13/8/2015 22:06	52	16/8/2015 7:11	60
7/8/2015 21:51	62	9/8/2015 10:56	61	9/8/2015 20:01	54	11/8/2015 21:06	62	13/8/2015 22:11	42	16/8/2015 7:16	60
7/8/2015 21:56	43	9/8/2015 11:01	61	9/8/2015 20:06	51	11/8/2015 21:11	62	13/8/2015 22:16	54	16/8/2015 7:21	60
7/8/2015 22:01	61	9/8/2015 11:06	61	9/8/2015 20:11	49	11/8/2015 21:16	62	13/8/2015 22:21	52	16/8/2015 7:26	60
7/8/2015 22:06	62	9/8/2015 11:11	61	9/8/2015 20:16	48	11/8/2015 21:21	62	13/8/2015 22:26	62	16/8/2015 7:31	61
7/8/2015 22:11	49	9/8/2015 11:16	61	9/8/2015 20:21	40	11/8/2015 21:26	61	13/8/2015 22:31	61	16/8/2015 7:36	60
7/8/2015 22:16	61	9/8/2015 11:21	62	9/8/2015 20:26	71	11/8/2015 21:31	62	13/8/2015 22:36	62	16/8/2015 7:41	60
7/8/2015 22:21	61	9/8/2015 11:26	62	9/8/2015 20:31	66	11/8/2015 21:36	61	13/8/2015 22:41	43	16/8/2015 7:46	61
7/8/2015 22:26	61	9/8/2015 11:31	60	9/8/2015 20:36	58	11/8/2015 21:41	61	13/8/2015 22:46	49	16/8/2015 7:51	61
7/8/2015 22:31	61	9/8/2015 11:36	61	9/8/2015 20:41	59	11/8/2015 21:46	61	13/8/2015 22:51	62	16/8/2015 7:56	53
7/8/2015 22:36	62	9/8/2015 11:41	61	9/8/2015 20:46	57	11/8/2015 21:51	61	13/8/2015 22:56	62	16/8/2015 8:01	61
7/8/2015 22:41	49	9/8/2015 11:46	60	9/8/2015 20:51	56	11/8/2015 21:56	62	14/8/2015 19:01	62	16/8/2015 8:06	61
7/8/2015 22:46	61	9/8/2015 11:51	61	9/8/2015 20:56	64	11/8/2015 22:01	62	14/8/2015 19:06	61	16/8/2015 8:11	61
7/8/2015 22:51	61	9/8/2015 11:56	61	9/8/2015 21:01	61	11/8/2015 22:06	62	14/8/2015 19:11	61	16/8/2015 8:16	61
7/8/2015 22:56	61	9/8/2015 12:01	61	9/8/2015 21:06	68	11/8/2015 22:11	62	14/8/2015 19:16	61	16/8/2015 8:21	61
8/8/2015 19:01	62	9/8/2015 12:06	61	9/8/2015 21:11	61	11/8/2015 22:16	62	14/8/2015 19:21	61	16/8/2015 8:26	61
8/8/2015 19:06	60	9/8/2015 12:11	61	9/8/2015 21:16	59	11/8/2015 22:21	61	14/8/2015 19:26	61	16/8/2015 8:31	61
8/8/2015 19:11	62	9/8/2015 12:16	61	9/8/2015 21:21	57	11/8/2015 22:26	62	14/8/2015 19:31	61	16/8/2015 8:36	62
8/8/2015 19:16	51	9/8/2015 12:21	61	9/8/2015 21:26	56	11/8/2015 22:31	62	14/8/2015 19:36	55	16/8/2015 8:41	62
8/8/2015 19:21	46	9/8/2015 12:26	47	9/8/2015 21:31	57	11/8/2015 22:36	61	14/8/2015 19:41	54	16/8/2015 8:46	61
8/8/2015 19:26	56	9/8/2015 12:31	60	9/8/2015 21:36	59	11/8/2015 22:41	55	14/8/2015 19:46	53	16/8/2015 8:51	61
8/8/2015 19:31	54	9/8/2015 12:36	61	9/8/2015 21:41	58	11/8/2015 22:46	58	14/8/2015 19:51	56	16/8/2015 8:56	61
8/8/2015 19:36	62	9/8/2015 12:41	60	9/8/2015 21:46	57	11/8/2015 22:51	61	14/8/2015 19:56	57	16/8/2015 9:01	61
8/8/2015 19:41	43	9/8/2015 12:46	61	9/8/2015 21:51	58	11/8/2015 22:56	61	14/8/2015 20:01	56	16/8/2015 9:06	49
8/8/2015 19:46	52	9/8/2015 12:51	61	9/8/2015 21:56	59	12/8/2015 19:01	64	14/8/2015 20:06	55	16/8/2015 9:11	44
8/8/2015 19:51	62	9/8/2015 12:56	62	9/8/2015 22:01	59	12/8/2015 19:06	59	14/8/2015 20:11	56	16/8/2015 9:16	50
8/8/2015 19:56	50	9/8/2015 13:01	61	9/8/2015 22:06	57	12/8/2015 19:11	60	14/8/2015 20:16	50	16/8/2015 9:21	62
8/8/2015 20:01	49	9/8/2015 13:06	61	9/8/2015 22:11	57	12/8/2015 19:16	61	14/8/2015 20:21	56	16/8/2015 9:26	54
8/8/2015 20:06	53	9/8/2015 13:11	61	9/8/2015 22:16	54	12/8/2015 19:21	61	14/8/2015 20:26	52	16/8/2015 9:31	54
8/8/2015 20:11	57	9/8/2015 13:16	61	9/8/2015 22:21	56	12/8/2015 19:26	49	14/8/2015 20:31	52	16/8/2015 9:36	54
8/8/2015 20:16	52	9/8/2015 13:21	61	9/8/2015 22:26	57	12/8/2015 19:31	54	14/8/2015 20:36	49	16/8/2015 9:41	50
8/8/2015 20:21	61	9/8/2015 13:26	61	9/8/2015 22:31	54	12/8/2015 19:36	54	14/8/2015 20:41	55	16/8/2015 9:46	51
8/8/2015 20:26	62	9/8/2015 13:31	61	9/8/2015 22:36	50	12/8/2015 19:41	51	14/8/2015 20:46	51	16/8/2015 9:51	56
8/8/2015 20:31	62	9/8/2015 13:36	61	9/8/2015 22:41	48	12/8/2015 19:46	52	14/8/2015 20:51	62	16/8/2015 9:56	51
8/8/2015 20:36	62	9/8/2015 13:41	61	9/8/2015 22:46	62	12/8/2015 19:51	50	14/8/2015 20:56	49	16/8/2015 10:01	55
8/8/2015 20:41	62	9/8/2015 13:46	46	9/8/2015 22:51	61	12/8/2015 19:56	53	14/8/2015 21:01	54	16/8/2015 10:06	59
8/8/2015 20:46	56	9/8/2015 13:51	43	9/8/2015 22:56	61	12/8/2015 20:01	55	14/8/2015 21:06	62	16/8/2015 10:11	55
8/8/2015 20:51	53	9/8/2015 13:56	61	10/8/2015 19:01	54	12/8/2015 20:06	50	14/8/2015 21:11	62	16/8/2015 10:16	53
8/8/2015 20:56	62	9/8/2015 14:01	43	10/8/2015 19:06	53	12/8/2015 20:11	59	14/8/2015 21:16	62	16/8/2015 10:21	49
8/8/2015 21:01	62	9/8/2015 14:06	40	10/8/2015 19:11	52	12/8/2015 20:16	59	14/8/2015 21:21	52	16/8/2015 10:26	51
8/8/2015 21:06	62	9/8/2015 14:11	52	10/8/2015 19:16	57	12/8/2015 20:21	56	14/8/2015 21:26	62	16/8/2015 10:31	53
8/8/2015 21:11	61	9/8/2015 14:16	62	10/8/2015 19:21	54	12/8/2015 20:26	54	14/8/2015 21:31	47	16/8/2015 10:36	54
8/8/2015 21:16	62	9/8/2015 14:21	62	10/8/2015 19:26	57	12/8/2015 20:31	53	14/8/2015 21:36	47	16/8/2015 10:41	53
8/8/2015 21:21	62	9/8/2015 14:26	61	10/8/2015 19:31	56	12/8/2015 20:36	49	14/8/2015 21:41	54	16/8/2015 10:46	55
8/8/2015 21:26	62	9/8/2015 14:31	52	10/8/2015 19:36	52	12/8/2015 20:41	51	14/8/2015 21:46	62	16/8/2015 10:51	50
8/8/2015 21:31	62	9/8/2015 14:36	61	10/8/2015 19:41	47	12/8/2015 20:46	39	14/8/2015 21:51	62	16/8/2015 10:56	55
8/8/2015 21:36	52	9/8/2015 14:41	61	10/8/2015 19:46	55	12/8/2015 20:51	61	14/8/2015 21:56	53	16/8/2015 11:01	43
8/8/2015 21:41	62	9/8/2015 14:46	61	10/8/2015 19:51	56	12/8/2015 20:56	62	14/8/2015 22:01	53	16/8/2015 11:06	61
8/8/2015 21:46	62	9/8/2015 14:51	61	10/8/2015 19:56	54	12/8/2015 21:01	51	14/8/2015 22:06	62	16/8/2015 11:11	51
8/8/2015 21:51	62	9/8/2015 14:56	62	10/8/2015 20:01	44	12/8/2015 21:06	62	14/8/2015 22:11	62	16/8/2015 11:16	48
8/8/2015 21:56	62	9/8/2015 15:01	61	10/8/2015 20:06	54	12/8/2015 21:11	62	14/8/2015 22:16	62	16/8/2015 11:21	55
8/8/2015 22:01	61	9/8/2015 15:06	61	10/8/2015 20:11	48	12/8/2015 21:16	62	14/8/2015 22:21	62	16/8/2015 11:26	52
8/8/2015 22:06	62	9/8/2015 15:11	56	10/8/2015 20:16	62	12/8/2015 21:21	62	14/8/2015 22:26	42	16/8/2015 11:31	46
8/8/2015 22:11	61	9/8/2015 15:16	61	10/8/2015 20:21	52	12/8/2015 21:26	61	14/8/2015 22:31	49	16/8/2015 11:36	51
8/8/2015 22:16	53	9/8/2015 15:21	61	10/8/2015 20:26	55	12/8/2015 21:31	62	14/8/2015 22:36	62	16/8/2015 11:41	36
8/8/2015 22:21	55	9/8/2015 15:26	62	10/8/2015 20:31	43	12/8/2015 21:36	61	14/8/2015 22:41	53	16/8/2015 11:46	62
8/8/2015 22:26	59	9/8/2015 15:31	61	10/8/2015 20:36	47	12/8/2015 21:41	61	14/8/2015 22:46	62	16/8/2015 11:51	62
8/8/2015 22:31	62	9/8/2015 15:36	62	10/8/2015 20:41	62	12/8/2015 21:46	61	14/8/2015 22:51	62	16/8/2015 11:56	47
8/8/2015 22:36	54	9/8/2015 15:41	61	10/8/2015 20:46	44	12/8/2015 21:51	62	14/8/2015 22:56	62	16/8/2015 12:01	62
8/8/2015 22:41	62	9/8/2015 15:46	61	10/8/2015 20:51	43	12/8/2015 21:56	46	15/8/2015 19:01	56	16/8/2015 12:06	50
8/8/2015 22:46	61	9/8/2015 15:51	49	10/8/2015 20:56	62	12/8/2015 22:01	61	15/8/2015 19:06	59	16/8/2015 12:11	61
8/8/2015 22:51	61	9/8/2015 15:56	61	10/8/2015 21:01	62	12/8/2015 22:06	39	15/8/2015 19:11	56	16/8/2015 12:16	62
8/8/2015 22:56	51	9/8/2015 16:01	62	10/8/2015 21:06	50	12/8/2015 22:11	61	15/8/2015 19:16	51	16/8/2015 12:21	62
9/8/2015 7:01	60	9/8/2015 16:06	62	10/8/2015 21:11	62	12/8/2015 22:16	61	15/8/2015 19:21	54	16/8/2015 12:26	62
9/8/2015 7:06	61	9/8/2015 16:11	61	10/8/2015 21:16	62	12/8/2015 22:21	61	15/8/2015 19:26	52	16/8/2015 12:31	46
9/8/2015 7:11	61	9/8/2015 16:16	61	10/8/2015 21:21	62	12/8/2015 22:26	55	15/8/2015 19:31	51	16/8/2015 12:36	52

Real-time Noise Data	RTN2a (Hong Kong Electric Centre)						
16/8/2015 15:31	52	17/8/2015 20:36	59	19/8/2015 21:41	62	21/8/2015 22:46	43
16/8/2015 15:36	54	17/8/2015 20:41	59	19/8/2015 21:46	54	21/8/2015 22:51	57
16/8/2015 15:41	55	17/8/2015 20:46	58	19/8/2015 21:51	61	21/8/2015 22:56	62
16/8/2015 15:46	49	17/8/2015 20:51	55	19/8/2015 21:56	54	22/8/2015 19:01	54
16/8/2015 15:51	57	17/8/2015 20:56	58	19/8/2015 22:01	62	22/8/2015 19:06	46
16/8/2015 15:56	55	17/8/2015 21:01	59	19/8/2015 22:06	61	22/8/2015 19:11	46
16/8/2015 16:01	53	17/8/2015 21:06	60	19/8/2015 22:11	62	22/8/2015 19:16	49
16/8/2015 16:06	51	17/8/2015 21:11	60	19/8/2015 22:16	53	22/8/2015 19:21	52
16/8/2015 16:11	62	17/8/2015 21:16	59	19/8/2015 22:21	62	22/8/2015 19:26	53
16/8/2015 16:16	43	17/8/2015 21:21	58	19/8/2015 22:26	61	22/8/2015 19:31	55
16/8/2015 16:21	53	17/8/2015 21:26	54	19/8/2015 22:31	61	22/8/2015 19:36	52
16/8/2015 16:26	62	17/8/2015 21:31	58	19/8/2015 22:36	61	22/8/2015 19:41	50
16/8/2015 16:31	62	17/8/2015 21:36	60	19/8/2015 22:41	62	22/8/2015 19:46	49
16/8/2015 16:36	55	17/8/2015 21:41	57	19/8/2015 22:46	61	22/8/2015 19:51	55
16/8/2015 16:41	62	17/8/2015 21:46	57	19/8/2015 22:51	53	22/8/2015 19:56	62
16/8/2015 16:46	52	17/8/2015 21:51	58	19/8/2015 22:56	61	22/8/2015 20:01	62
16/8/2015 16:51	51	17/8/2015 21:56	55	20/8/2015 19:01	53	22/8/2015 20:06	57
16/8/2015 16:56	55	17/8/2015 22:01	52	20/8/2015 19:06	62	22/8/2015 20:11	62
16/8/2015 17:01	53	17/8/2015 22:06	55	20/8/2015 19:11	61	22/8/2015 20:16	62
16/8/2015 17:06	52	17/8/2015 22:11	47	20/8/2015 19:16	50	22/8/2015 20:21	62
16/8/2015 17:11	53	17/8/2015 22:16	61	20/8/2015 19:21	54	22/8/2015 20:26	61
16/8/2015 17:16	48	17/8/2015 22:21	56	20/8/2015 19:26	53	22/8/2015 20:31	61
16/8/2015 17:21	49	17/8/2015 22:26	48	20/8/2015 19:31	54	22/8/2015 20:36	62
16/8/2015 17:26	44	17/8/2015 22:31	51	20/8/2015 19:36	57	22/8/2015 20:41	43
16/8/2015 17:31	62	17/8/2015 22:36	54	20/8/2015 19:41	54	22/8/2015 20:46	61
16/8/2015 17:36	45	17/8/2015 22:41	57	20/8/2015 19:46	54	22/8/2015 20:51	61
16/8/2015 17:41	39	17/8/2015 22:46	44	20/8/2015 19:51	54	22/8/2015 20:56	61
16/8/2015 17:46	62	17/8/2015 22:51	48	20/8/2015 19:56	51	22/8/2015 21:01	61
16/8/2015 17:51	50	17/8/2015 22:56	61	20/8/2015 20:01	54	22/8/2015 21:06	42
16/8/2015 17:56	62	18/8/2015 19:01	52	20/8/2015 20:06	58	22/8/2015 21:11	61
16/8/2015 18:01	53	18/8/2015 19:06	52	20/8/2015 20:11	44	22/8/2015 21:16	62
16/8/2015 18:06	51	18/8/2015 19:11	49	20/8/2015 20:16	54	22/8/2015 21:21	61
16/8/2015 18:11	39	18/8/2015 19:16	57	20/8/2015 20:21	53	22/8/2015 21:26	61
16/8/2015 18:16	53	18/8/2015 19:21	54	20/8/2015 20:26	50	22/8/2015 21:31	61
16/8/2015 18:21	51	18/8/2015 19:26	57	20/8/2015 20:31	42	22/8/2015 21:36	61
16/8/2015 18:26	49	18/8/2015 19:31	54	20/8/2015 20:36	46	22/8/2015 21:41	62
16/8/2015 18:31	47	18/8/2015 19:36	55	20/8/2015 20:41	53	22/8/2015 21:46	61
16/8/2015 18:36	62	18/8/2015 19:41	52	20/8/2015 20:46	48	22/8/2015 21:51	61
16/8/2015 18:41	46	18/8/2015 19:46	48	20/8/2015 20:51	57	22/8/2015 21:56	62
16/8/2015 18:46	51	18/8/2015 19:51	51	20/8/2015 20:56	51	22/8/2015 22:01	40
16/8/2015 18:51	45	18/8/2015 19:56	50	20/8/2015 21:01	62	22/8/2015 22:06	62
16/8/2015 18:56	62	18/8/2015 20:01	62	20/8/2015 21:06	44	22/8/2015 22:11	61
16/8/2015 19:01	50	18/8/2015 20:06	53	20/8/2015 21:11	42	22/8/2015 22:16	61
16/8/2015 19:06	52	18/8/2015 20:11	54	20/8/2015 21:16	50	22/8/2015 22:21	61
16/8/2015 19:11	62	18/8/2015 20:16	62	20/8/2015 21:21	62	22/8/2015 22:26	61
16/8/2015 19:16	62	18/8/2015 20:21	62	20/8/2015 21:26	62	22/8/2015 22:31	62
16/8/2015 19:21	62	18/8/2015 20:26	62	20/8/2015 21:31	61	22/8/2015 22:36	61
16/8/2015 19:26	62	18/8/2015 20:31	63	20/8/2015 21:36	61	22/8/2015 22:41	61
16/8/2015 19:31	62	18/8/2015 20:36	39	20/8/2015 21:41	61	22/8/2015 22:46	61
16/8/2015 19:36	62	18/8/2015 20:41	61	20/8/2015 21:46	61	22/8/2015 22:51	61
16/8/2015 19:41	62	18/8/2015 20:46	62	20/8/2015 21:51	62	22/8/2015 22:56	49
16/8/2015 19:46	62	18/8/2015 20:51	53	20/8/2015 21:56	61	23/8/2015 7:01	61
16/8/2015 19:51	39	18/8/2015 20:56	40	20/8/2015 22:01	54	23/8/2015 7:06	60
16/8/2015 19:56	62	18/8/2015 21:01	62	20/8/2015 22:06	48	23/8/2015 7:11	61
16/8/2015 20:01	62	18/8/2015 21:06	62	20/8/2015 22:11	39	23/8/2015 7:16	60
16/8/2015 20:06	62	18/8/2015 21:11	62	20/8/2015 22:16	51	23/8/2015 7:21	56
16/8/2015 20:11	62	18/8/2015 21:16	62	20/8/2015 22:21	62	23/8/2015 7:26	56
16/8/2015 20:16	62	18/8/2015 21:21	62	20/8/2015 22:26	54	23/8/2015 7:31	60
16/8/2015 20:21	62	18/8/2015 21:26	61	20/8/2015 22:31	61	23/8/2015 7:36	60
16/8/2015 20:26	61	18/8/2015 21:31	62	20/8/2015 22:36	42	23/8/2015 7:41	60
16/8/2015 20:31	62	18/8/2015 21:36	62	20/8/2015 22:41	47	23/8/2015 7:46	61
16/8/2015 20:36	61	18/8/2015 21:41	61	20/8/2015 22:46	62	23/8/2015 7:51	60
16/8/2015 20:41	61	18/8/2015 21:46	61	20/8/2015 22:51	40	23/8/2015 7:56	61
16/8/2015 20:46	61	18/8/2015 21:51	61	20/8/2015 22:56	61	23/8/2015 8:01	61
16/8/2015 20:51	61	18/8/2015 21:56	61	21/8/2015 19:01	57	23/8/2015 8:06	61
16/8/2015 20:56	61	18/8/2015 22:01	61	21/8/2015 19:06	62	23/8/2015 8:11	62
16/8/2015 21:01	62	18/8/2015 22:06	62	21/8/2015 19:11	62	23/8/2015 8:16	61
16/8/2015 21:06	52	18/8/2015 22:11	61	21/8/2015 19:16	61	23/8/2015 8:21	61
16/8/2015 21:11	43	18/8/2015 22:16	56	21/8/2015 19:21	49	23/8/2015 8:26	61
16/8/2015 21:16	62	18/8/2015 22:21	61	21/8/2015 19:26	62	23/8/2015 8:31	61
16/8/2015 21:21	62	18/8/2015 22:26	62	21/8/2015 19:31	62	23/8/2015 8:36	61
16/8/2015 21:26	62	18/8/2015 22:31	61	21/8/2015 19:36	36	23/8/2015 8:41	61
16/8/2015 21:31	61	18/8/2015 22:36	61	21/8/2015 19:41	52	23/8/2015 8:46	61
16/8/2015 21:36	62	18/8/2015 22:41	61	21/8/2015 19:46	46	23/8/2015 8:51	62
16/8/2015 21:41	61	18/8/2015 22:46	61	21/8/2015 19:51	55	23/8/2015 8:56	49
16/8/2015 21:46	61	18/8/2015 22:51	55	21/8/2015 19:56	60	23/8/2015 9:01	62
16/8/2015 21:51	61	18/8/2015 22:56	52	21/8/2015 20:01	58	23/8/2015 9:06	43
16/8/2015 21:56	61	19/8/2015 19:01	61	21/8/2015 20:06	58	23/8/2015 9:11	56
16/8/2015 22:01	62	19/8/2015 19:06	61	21/8/2015 20:11	46	23/8/2015 9:16	52
16/8/2015 22:06	62	19/8/2015 19:11	61	21/8/2015 20:16	55	23/8/2015 9:21	50
16/8/2015 22:11	49	19/8/2015 19:16	60	21/8/2015 20:21	57	23/8/2015 9:26	48
16/8/2015 22:16	61	19/8/2015 19:21	60	21/8/2015 20:26	58	23/8/2015 9:31	36
16/8/2015 22:21	62	19/8/2015 19:26	61	21/8/2015 20:31	58	23/8/2015 9:36	62
16/8/2015 22:26	61	19/8/2015 19:31	51	21/8/2015 20:36	57	23/8/2015 9:41	62
16/8/2015 22:31	61	19/8/2015 19:36	62	21/8/2015 20:41	56	23/8/2015 9:46	61
16/8/2015 22:36	61	19/8/2015 19:41	61	21/8/2015 20:46	56	23/8/2015 9:51	61
16/8/2015 22:41	62	19/8/2015 19:46	62	21/8/2015 20:51	51	23/8/2015 9:56	61
16/8/2015 22:46	61	19/8/2015 19:51	47	21/8/2015 20:56	53	23/8/2015 10:01	52
16/8/2015 22:51	61	19/8/2015 19:56	51	21/8/2015 21:01	62	23/8/2015 10:06	50
16/8/2015 22:56	62	19/8/2015 20:01	59	21/8/2015 21:06	51	23/8/2015 10:11	61
17/8/2015 19:01	59	19/8/2015 20:06	62	21/8/2015 21:11	53	23/8/2015 10:16	61
17/8/2015 19:06	58	19/8/2015 20:11	62	21/8/2015 21:16	52	23/8/2015 10:21	62
17/8/2015 19:11	59	19/8/2015 20:16	62	21/8/2015 21:21	62	23/8/2015 10:26	61
17/8/2015 19:16	60	19/8/2015 20:21	46	21/8/2015 21:26	49	23/8/2015 10:31	61
17/8/2015 19:21	58	19/8/2015 20:26	54	21/8/2015 21:31	42	23/8/2015 10:36	61
17/8/2015 19:26	58	19/8/2015 20:31	62	21/8/2015 21:36	61	23/8/2015 10:41	61
17/8/2015 19:31	59	19/8/2015 20:36	50	21/8/2015 21:41	50	23/8/2015 10:46	47
17/8/2015 19:36	59	19/8/2015 20:41	52	21/8/2015 21:46	60	23/8/2015 10:51	61
17/8/2015 19:41	56	19/8/2015 20:46	53	21/8/2015 21:51	62	23/8/2015 10:56	39
17/8/2015 19:46	59	19/8/2015 20:51	54	21/8/2015 21:56	62	23/8/2015 11:01	62
17/8/2015 19:51	59	19/8/2015 20:56	62	21/8/2015 22:01	61	23/8/2015 11:06	45
17/8/2015 19:56	58	19/8/2015 21:01	54	21/8/2015 22:06	62	23/8/2015 11:11	46
17/8/2015 20:01	57	19/8/2015 21:06	55	21/8/2015 22:11	54	23/8/2015 11:16	62
17/8/2015 20:06	55	19/8/2015 21:11	43	21/8/2015 22:16	51	23/8/2015 11:21	53
17/8/2015 20:11	60	19/8/2015 21:16	50	21/8/2015 22:21	61	23/8/2015 11:26	62
17/8/2015 20:16	58	19/8/2015 21:21	50	21/8/2015 22:26	52	23/8/2015 11:31	61
17/8/2015 20:21	57	19/8/2015 21:26	62	21/8/2015 22:31	62	23/8/2015 11:36	60
17/8/2015 20:26	59	19/8/2015 21:31	62	21/8/2015 22:36	62	23/8/2015 11:41	61
17/8/2015 20:31	56	19/8/2015 21:36	62	21/8/2015 22:41	62	23/8/2015 11:46	48

Real-time Noise Data	RTN2a (Hong Kong Electric Centre)												
25/8/2015 22:01	57		29/7/2015 0:51	55		30/7/2015 1:56	51		31/7/2015 3:01	57		1/8/2015 4:06	58
25/8/2015 22:06	62		29/7/2015 0:56	51		30/7/2015 2:01	58		31/7/2015 3:06	57		1/8/2015 4:11	42
25/8/2015 22:11	61		29/7/2015 1:01	51		30/7/2015 2:06	58		31/7/2015 3:11	58		1/8/2015 4:16	58
25/8/2015 22:16	64		29/7/2015 1:06	53		30/7/2015 2:11	58		31/7/2015 3:16	57		1/8/2015 4:21	58
25/8/2015 22:21	63		29/7/2015 1:11	52		30/7/2015 2:16	58		31/7/2015 3:21	57		1/8/2015 4:26	58
25/8/2015 22:26	69		29/7/2015 1:16	50		30/7/2015 2:21	58		31/7/2015 3:26	58		1/8/2015 4:31	57
25/8/2015 22:31	42		29/7/2015 1:21	55		30/7/2015 2:26	57		31/7/2015 3:31	57		1/8/2015 4:36	58
25/8/2015 22:36	61		29/7/2015 1:26	49		30/7/2015 2:31	57		31/7/2015 3:36	57		1/8/2015 4:41	58
25/8/2015 22:41	62		29/7/2015 1:31	39		30/7/2015 2:36	57		31/7/2015 3:41	57		1/8/2015 4:46	58
25/8/2015 22:46	61		29/7/2015 1:36	45		30/7/2015 2:41	58		31/7/2015 3:46	56		1/8/2015 4:51	58
25/8/2015 22:51	61		29/7/2015 1:41	50		30/7/2015 2:46	58		31/7/2015 3:51	57		1/8/2015 4:56	58
25/8/2015 22:56	61		29/7/2015 1:46	45		30/7/2015 2:51	57		31/7/2015 3:56	58		1/8/2015 5:01	58
26/8/2015 19:01	55		29/7/2015 1:51	59		30/7/2015 2:56	58		31/7/2015 4:01	57		1/8/2015 5:06	58
26/8/2015 19:06	56		29/7/2015 1:56	58		30/7/2015 3:01	57		31/7/2015 4:06	58		1/8/2015 5:11	47
26/8/2015 19:11	58		29/7/2015 2:01	51		30/7/2015 3:06	57		31/7/2015 4:11	57		1/8/2015 5:16	58
26/8/2015 19:16	59		29/7/2015 2:06	58		30/7/2015 3:11	57		31/7/2015 4:16	56		1/8/2015 5:21	58
26/8/2015 19:21	57		29/7/2015 2:11	50		30/7/2015 3:16	57		31/7/2015 4:21	56		1/8/2015 5:26	58
26/8/2015 19:26	60		29/7/2015 2:16	58		30/7/2015 3:21	57		31/7/2015 4:26	57		1/8/2015 5:31	58
26/8/2015 19:31	51		29/7/2015 2:21	58		30/7/2015 3:26	57		31/7/2015 4:31	57		1/8/2015 5:36	41
26/8/2015 19:36	57		29/7/2015 2:26	58		30/7/2015 3:31	57		31/7/2015 4:36	57		1/8/2015 5:41	46
26/8/2015 19:41	53		29/7/2015 2:31	48		30/7/2015 3:36	56		31/7/2015 4:41	57		1/8/2015 5:46	58
26/8/2015 19:46	52		29/7/2015 2:36	57		30/7/2015 3:41	57		31/7/2015 4:46	57		1/8/2015 5:51	58
26/8/2015 19:51	56		29/7/2015 2:41	57		30/7/2015 3:46	57		31/7/2015 4:51	57		1/8/2015 5:56	53
26/8/2015 19:56	57		29/7/2015 2:46	57		30/7/2015 3:51	57		31/7/2015 4:56	57		1/8/2015 6:01	51
26/8/2015 20:01	63		29/7/2015 2:51	57		30/7/2015 3:56	57		31/7/2015 5:01	56		1/8/2015 6:06	40
26/8/2015 20:06	58		29/7/2015 2:56	57		30/7/2015 4:01	56		31/7/2015 5:06	57		1/8/2015 6:11	51
26/8/2015 20:11	54		29/7/2015 3:01	58		30/7/2015 4:06	57		31/7/2015 5:11	57		1/8/2015 6:16	53
26/8/2015 20:16	42		29/7/2015 3:06	57		30/7/2015 4:11	58		31/7/2015 5:16	57		1/8/2015 6:21	53
26/8/2015 20:21	57		29/7/2015 3:11	41		30/7/2015 4:16	54		31/7/2015 5:21	57		1/8/2015 6:26	50
26/8/2015 20:26	50		29/7/2015 3:16	57		30/7/2015 4:21	58		31/7/2015 5:26	57		1/8/2015 6:31	54
26/8/2015 20:31	54		29/7/2015 3:21	57		30/7/2015 4:26	56		31/7/2015 5:31	58		1/8/2015 6:36	55
26/8/2015 20:36	47		29/7/2015 3:26	57		30/7/2015 4:31	57		31/7/2015 5:36	46		1/8/2015 6:41	55
26/8/2015 20:41	43		29/7/2015 3:31	57		30/7/2015 4:36	57		31/7/2015 5:41	58		1/8/2015 6:46	57
26/8/2015 20:46	53		29/7/2015 3:36	57		30/7/2015 4:41	57		31/7/2015 5:46	58		1/8/2015 6:51	57
26/8/2015 20:51	46		29/7/2015 3:41	56		30/7/2015 4:46	57		31/7/2015 5:51	48		1/8/2015 6:56	58
26/8/2015 20:56	62		29/7/2015 3:46	57		30/7/2015 4:51	57		31/7/2015 5:56	49		1/8/2015 7:01	58
26/8/2015 21:01	62		29/7/2015 3:51	57		30/7/2015 4:56	56		31/7/2015 6:01	45		1/8/2015 7:06	59
26/8/2015 21:06	62		29/7/2015 3:56	57		30/7/2015 5:01	58		31/7/2015 6:06	45		1/8/2015 7:11	58
26/8/2015 21:11	61		29/7/2015 4:01	57		30/7/2015 5:06	57		31/7/2015 6:11	51		1/8/2015 7:16	59
26/8/2015 21:16	61		29/7/2015 4:06	57		30/7/2015 5:11	57		31/7/2015 6:16	52		1/8/2015 7:21	57
26/8/2015 21:21	62		29/7/2015 4:11	57		30/7/2015 5:16	58		31/7/2015 6:21	55		1/8/2015 7:26	57
26/8/2015 21:26	45		29/7/2015 4:16	57		30/7/2015 5:21	57		31/7/2015 6:26	55		1/8/2015 7:31	57
26/8/2015 21:31	62		29/7/2015 4:21	57		30/7/2015 5:26	40		31/7/2015 6:31	56		1/8/2015 7:36	61
26/8/2015 21:36	62		29/7/2015 4:26	56		30/7/2015 5:31	58		31/7/2015 6:36	57		1/8/2015 7:41	58
26/8/2015 21:41	62		29/7/2015 4:31	57		30/7/2015 5:36	50		31/7/2015 6:41	57		1/8/2015 7:46	56
26/8/2015 21:46	48		29/7/2015 4:36	58		30/7/2015 5:41	53		31/7/2015 6:46	59		1/8/2015 7:51	55
26/8/2015 21:51	62		29/7/2015 4:41	57		30/7/2015 5:46	47		31/7/2015 6:51	59		1/8/2015 7:56	58
26/8/2015 21:56	62		29/7/2015 4:46	57		30/7/2015 5:51	47		31/7/2015 6:56	59		2/8/2015 0:01	56
26/8/2015 22:01	61		29/7/2015 4:51	57		30/7/2015 5:56	54		31/7/2015 7:01	58		2/8/2015 0:06	56
26/8/2015 22:06	61		29/7/2015 4:56	57		30/7/2015 6:01	47		31/7/2015 7:06	59		2/8/2015 0:11	56
26/8/2015 22:11	61		29/7/2015 5:01	57		30/7/2015 6:06	54		31/7/2015 7:11	59		2/8/2015 0:16	57
26/8/2015 22:16	62		29/7/2015 5:06	57		30/7/2015 6:11	55		31/7/2015 7:16	58		2/8/2015 0:21	54
26/8/2015 22:21	43		29/7/2015 5:11	57		30/7/2015 6:16	54		31/7/2015 7:21	59		2/8/2015 0:26	55
26/8/2015 22:26	61		29/7/2015 5:16	57		30/7/2015 6:21	55		31/7/2015 7:26	59		2/8/2015 0:31	55
26/8/2015 22:31	62		29/7/2015 5:21	57		30/7/2015 6:26	56		31/7/2015 7:31	59		2/8/2015 0:36	54
26/8/2015 22:36	61		29/7/2015 5:26	58		30/7/2015 6:31	57		31/7/2015 7:36	58		2/8/2015 0:41	52
26/8/2015 22:41	61		29/7/2015 5:31	57		30/7/2015 6:36	57		31/7/2015 7:41	58		2/8/2015 0:46	56
26/8/2015 22:46	61		29/7/2015 5:36	49		30/7/2015 6:41	57		31/7/2015 7:46	58		2/8/2015 0:51	54
26/8/2015 22:51	61		29/7/2015 5:41	42		30/7/2015 6:46	57		31/7/2015 7:51	57		2/8/2015 0:56	55
26/8/2015 22:56	61		29/7/2015 5:46	43		30/7/2015 6:51	59		31/7/2015 7:56	58		2/8/2015 1:01	52
27/8/2015 19:01	61		29/7/2015 5:51	47		30/7/2015 6:56	59		1/8/2015 0:01	58		2/8/2015 1:06	53
27/8/2015 19:06	49		29/7/2015 5:56	58		30/7/2015 7:01	58		1/8/2015 0:06	59		2/8/2015 1:11	53
27/8/2015 19:11	61		29/7/2015 6:01	49		30/7/2015 7:06	58		1/8/2015 0:11	56		2/8/2015 1:16	52
27/8/2015 19:16	60		29/7/2015 6:06	52		30/7/2015 7:11	58		1/8/2015 0:16	56		2/8/2015 1:21	51
27/8/2015 19:21	61		29/7/2015 6:11	54		30/7/2015 7:16	58		1/8/2015 0:21	57		2/8/2015 1:26	52
27/8/2015 19:26	62		29/7/2015 6:16	57		30/7/2015 7:21	57		1/8/2015 0:26	56		2/8/2015 1:31	52
27/8/2015 19:31	62		29/7/2015 6:21	56		30/7/2015 7:26	58		1/8/2015 0:31	57		2/8/2015 1:36	54
27/8/2015 19:36	50		29/7/2015 6:26	56		30/7/2015 7:31	58		1/8/2015 0:36	56		2/8/2015 1:41	47
27/8/2015 19:41	52		29/7/2015 6:31	57		30/7/2015 7:36	57		1/8/2015 0:41	56		2/8/2015 1:46	49
27/8/2015 19:46	46		29/7/2015 6:36	57		30/7/2015 7:41	56		1/8/2015 0:46	56		2/8/2015 1:51	53
27/8/2015 19:51	49		29/7/2015 6:41	58		30/7/2015 7:46	58		1/8/2015 0:51	55		2/8/2015 1:56	49
27/8/2015 19:56	54		29/7/2015 6:46	58		30/7/2015 7:51	56		1/8/2015 0:56	56		2/8/2015 2:01	53
27/8/2015 20:01	51		29/7/2015 6:51	60		30/7/2015 7:56	56		1/8/2015 1:01	55		2/8/2015 2:06	57
27/8/2015 20:06	52		29/7/2015 6:56	60		31/7/2015 0:01	55		1/8/2015 1:06	54		2/8/2015 2:11	51
27/8/2015 20:11	62		29/7/2015 7:01	62		31/7/2015 0:06	56		1/8/2015 1:11	54		2/8/2015 2:16	58
27/8/2015 20:16	40		29/7/2015 7:06	61		31/7/2015 0:11	56		1/8/2015 1:16	54		2/8/2015 2:21	49
27/8/2015 20:21	62		29/7/2015 7:11	61		31/7/2015 0:16	56		1/8/2015 1:21	54		2/8/2015 2:26	48
27/8/2015 20:26	49		29/7/2015 7:16	60		31/7/2015 0:21	56		1/8/2015 1:26	55		2/8/2015 2:31	48
27/8/2015 20:31	61		29/7/2015 7:21	57		31/7/2015 0:26	56		1/8/2015 1:31	55		2/8/2015 2:36	52
27/8/2015 20:36	62		29/7/2015 7:26	59		31/7/2015 0:31	56		1/8/2015 1:36	52		2/8/2015 2:41	58
27/8/2015 20:41	50		29/7/2015 7:31	57		31/7/2015 0:36	54		1/8/2015 1:41	54		2/8/2015 2:46	57
27/8/2015 20:46	62		29/7/2015 7:36	57</									

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
2/8/2015 5:11	58	3/8/2015 6:16	50	4/8/2015 23:21	58	6/8/2015 0:26	54	7/8/2015 1:31	58	8/8/2015 2:36	58
2/8/2015 5:16	58	3/8/2015 6:21	53	4/8/2015 23:26	59	6/8/2015 0:31	54	7/8/2015 1:36	58	8/8/2015 2:41	53
2/8/2015 5:21	57	3/8/2015 6:26	56	4/8/2015 23:31	58	6/8/2015 0:36	53	7/8/2015 1:41	58	8/8/2015 2:46	48
2/8/2015 5:26	57	3/8/2015 6:31	55	4/8/2015 23:36	57	6/8/2015 0:41	51	7/8/2015 1:46	58	8/8/2015 2:51	53
2/8/2015 5:31	57	3/8/2015 6:36	57	4/8/2015 23:41	57	6/8/2015 0:46	53	7/8/2015 1:51	57	8/8/2015 2:56	41
2/8/2015 5:36	58	3/8/2015 6:41	57	4/8/2015 23:46	57	6/8/2015 0:51	52	7/8/2015 1:56	58	8/8/2015 3:01	39
2/8/2015 5:41	58	3/8/2015 6:46	58	4/8/2015 23:51	56	6/8/2015 0:56	52	7/8/2015 2:01	58	8/8/2015 3:06	45
2/8/2015 5:46	58	3/8/2015 6:51	58	4/8/2015 23:56	56	6/8/2015 1:01	51	7/8/2015 2:06	57	8/8/2015 3:11	48
2/8/2015 5:51	58	3/8/2015 6:56	58	5/8/2015 0:01	57	6/8/2015 1:06	49	7/8/2015 2:11	57	8/8/2015 3:16	51
2/8/2015 5:56	50	3/8/2015 23:01	58	5/8/2015 0:06	55	6/8/2015 1:11	49	7/8/2015 2:16	57	8/8/2015 3:21	49
2/8/2015 6:01	57	3/8/2015 23:06	59	5/8/2015 0:11	56	6/8/2015 1:16	49	7/8/2015 2:21	57	8/8/2015 3:26	58
2/8/2015 6:06	45	3/8/2015 23:11	60	5/8/2015 0:16	57	6/8/2015 1:21	51	7/8/2015 2:26	57	8/8/2015 3:31	58
2/8/2015 6:11	50	3/8/2015 23:16	57	5/8/2015 0:21	56	6/8/2015 1:26	51	7/8/2015 2:31	57	8/8/2015 3:36	38
2/8/2015 6:16	54	3/8/2015 23:21	58	5/8/2015 0:26	55	6/8/2015 1:31	58	7/8/2015 2:36	57	8/8/2015 3:41	58
2/8/2015 6:21	51	3/8/2015 23:26	56	5/8/2015 0:31	54	6/8/2015 1:36	51	7/8/2015 2:41	57	8/8/2015 3:46	45
2/8/2015 6:26	44	3/8/2015 23:31	57	5/8/2015 0:36	52	6/8/2015 1:41	58	7/8/2015 2:46	57	8/8/2015 3:51	45
2/8/2015 6:31	51	3/8/2015 23:36	56	5/8/2015 0:41	53	6/8/2015 1:46	58	7/8/2015 2:51	56	8/8/2015 3:56	32
2/8/2015 6:36	57	3/8/2015 23:41	54	5/8/2015 0:46	53	6/8/2015 1:51	58	7/8/2015 2:56	57	8/8/2015 4:01	58
2/8/2015 6:41	52	3/8/2015 23:46	55	5/8/2015 0:51	53	6/8/2015 1:56	58	7/8/2015 3:01	56	8/8/2015 4:06	58
2/8/2015 6:46	57	3/8/2015 23:51	57	5/8/2015 0:56	49	6/8/2015 2:01	57	7/8/2015 3:06	57	8/8/2015 4:11	58
2/8/2015 6:51	55	3/8/2015 23:56	56	5/8/2015 1:01	54	6/8/2015 2:06	57	7/8/2015 3:11	57	8/8/2015 4:16	58
2/8/2015 6:56	56	4/8/2015 0:01	53	5/8/2015 1:06	50	6/8/2015 2:11	58	7/8/2015 3:16	56	8/8/2015 4:21	58
2/8/2015 23:01	58	4/8/2015 0:06	57	5/8/2015 1:11	54	6/8/2015 2:16	57	7/8/2015 3:21	56	8/8/2015 4:26	42
2/8/2015 23:06	58	4/8/2015 0:11	51	5/8/2015 1:16	44	6/8/2015 2:21	57	7/8/2015 3:26	56	8/8/2015 4:31	58
2/8/2015 23:11	56	4/8/2015 0:16	56	5/8/2015 1:21	44	6/8/2015 2:26	58	7/8/2015 3:31	56	8/8/2015 4:36	57
2/8/2015 23:16	58	4/8/2015 0:21	55	5/8/2015 1:26	50	6/8/2015 2:31	57	7/8/2015 3:36	57	8/8/2015 4:41	45
2/8/2015 23:21	58	4/8/2015 0:26	52	5/8/2015 1:31	50	6/8/2015 2:36	57	7/8/2015 3:41	57	8/8/2015 4:46	58
2/8/2015 23:26	56	4/8/2015 0:31	52	5/8/2015 1:36	49	6/8/2015 2:41	57	7/8/2015 3:46	56	8/8/2015 4:51	58
2/8/2015 23:31	57	4/8/2015 0:36	52	5/8/2015 1:41	58	6/8/2015 2:46	57	7/8/2015 3:51	56	8/8/2015 4:56	58
2/8/2015 23:36	55	4/8/2015 0:41	53	5/8/2015 1:46	57	6/8/2015 2:51	57	7/8/2015 3:56	57	8/8/2015 5:01	58
2/8/2015 23:41	58	4/8/2015 0:46	52	5/8/2015 1:51	58	6/8/2015 2:56	56	7/8/2015 4:01	57	8/8/2015 5:06	57
2/8/2015 23:46	53	4/8/2015 0:51	53	5/8/2015 1:56	58	6/8/2015 3:01	57	7/8/2015 4:06	56	8/8/2015 5:11	57
2/8/2015 23:51	53	4/8/2015 0:56	56	5/8/2015 2:01	58	6/8/2015 3:06	57	7/8/2015 4:11	57	8/8/2015 5:16	58
2/8/2015 23:56	52	4/8/2015 1:01	48	5/8/2015 2:06	58	6/8/2015 3:11	58	7/8/2015 4:16	57	8/8/2015 5:21	57
3/8/2015 0:01	55	4/8/2015 1:06	49	5/8/2015 2:11	41	6/8/2015 3:16	57	7/8/2015 4:21	56	8/8/2015 5:26	58
3/8/2015 0:06	52	4/8/2015 1:11	51	5/8/2015 2:16	58	6/8/2015 3:21	56	7/8/2015 4:26	56	8/8/2015 5:31	58
3/8/2015 0:11	56	4/8/2015 1:16	58	5/8/2015 2:21	58	6/8/2015 3:26	56	7/8/2015 4:31	57	8/8/2015 5:36	49
3/8/2015 0:16	51	4/8/2015 1:21	58	5/8/2015 2:26	58	6/8/2015 3:31	57	7/8/2015 4:36	56	8/8/2015 5:41	45
3/8/2015 0:21	55	4/8/2015 1:26	58	5/8/2015 2:31	57	6/8/2015 3:36	57	7/8/2015 4:41	57	8/8/2015 5:46	58
3/8/2015 0:26	54	4/8/2015 1:31	49	5/8/2015 2:36	57	6/8/2015 3:41	57	7/8/2015 4:46	57	8/8/2015 5:51	58
3/8/2015 0:31	52	4/8/2015 1:36	58	5/8/2015 2:41	57	6/8/2015 3:46	56	7/8/2015 4:51	57	8/8/2015 5:56	49
3/8/2015 0:36	51	4/8/2015 1:41	58	5/8/2015 2:46	57	6/8/2015 3:51	57	7/8/2015 4:56	56	8/8/2015 6:01	44
3/8/2015 0:41	46	4/8/2015 1:46	40	5/8/2015 2:51	57	6/8/2015 3:56	57	7/8/2015 5:01	57	8/8/2015 6:06	51
3/8/2015 0:46	44	4/8/2015 1:51	58	5/8/2015 2:56	58	6/8/2015 4:01	57	7/8/2015 5:06	57	8/8/2015 6:11	52
3/8/2015 0:51	49	4/8/2015 1:56	58	5/8/2015 3:01	57	6/8/2015 4:06	56	7/8/2015 5:11	57	8/8/2015 6:16	52
3/8/2015 0:56	49	4/8/2015 2:01	58	5/8/2015 3:06	58	6/8/2015 4:11	56	7/8/2015 5:16	56	8/8/2015 6:21	53
3/8/2015 1:01	47	4/8/2015 2:06	58	5/8/2015 3:11	57	6/8/2015 4:16	56	7/8/2015 5:21	57	8/8/2015 6:26	57
3/8/2015 1:06	52	4/8/2015 2:11	57	5/8/2015 3:16	57	6/8/2015 4:21	57	7/8/2015 5:26	57	8/8/2015 6:31	55
3/8/2015 1:11	58	4/8/2015 2:16	57	5/8/2015 3:21	56	6/8/2015 4:26	57	7/8/2015 5:31	57	8/8/2015 6:36	55
3/8/2015 1:16	37	4/8/2015 2:21	58	5/8/2015 3:26	57	6/8/2015 4:31	57	7/8/2015 5:36	58	8/8/2015 6:41	56
3/8/2015 1:21	49	4/8/2015 2:26	57	5/8/2015 3:31	57	6/8/2015 4:36	57	7/8/2015 5:41	58	8/8/2015 6:46	56
3/8/2015 1:26	58	4/8/2015 2:31	57	5/8/2015 3:36	56	6/8/2015 4:41	57	7/8/2015 5:46	58	8/8/2015 6:51	57
3/8/2015 1:31	58	4/8/2015 2:36	57	5/8/2015 3:41	56	6/8/2015 4:46	57	7/8/2015 5:51	58	8/8/2015 6:56	58
3/8/2015 1:36	58	4/8/2015 2:41	57	5/8/2015 3:46	56	6/8/2015 4:51	56	7/8/2015 5:56	46	8/8/2015 23:01	58
3/8/2015 1:41	58	4/8/2015 2:46	57	5/8/2015 3:51	57	6/8/2015 4:56	57	7/8/2015 6:01	58	8/8/2015 23:06	57
3/8/2015 1:46	57	4/8/2015 2:51	56	5/8/2015 3:56	57	6/8/2015 5:01	57	7/8/2015 6:06	52	8/8/2015 23:11	58
3/8/2015 1:51	57	4/8/2015 2:56	57	5/8/2015 4:01	56	6/8/2015 5:06	57	7/8/2015 6:11	55	8/8/2015 23:16	59
3/8/2015 1:56	58	4/8/2015 3:01	57	5/8/2015 4:06	56	6/8/2015 5:11	57	7/8/2015 6:16	57	8/8/2015 23:21	59
3/8/2015 2:01	57	4/8/2015 3:06	56	5/8/2015 4:11	57	6/8/2015 5:16	56	7/8/2015 6:21	55	8/8/2015 23:26	58
3/8/2015 2:06	57	4/8/2015 3:11	57	5/8/2015 4:16	57	6/8/2015 5:21	57	7/8/2015 6:26	56	8/8/2015 23:31	57
3/8/2015 2:11	58	4/8/2015 3:16	57	5/8/2015 4:21	57	6/8/2015 5:26	57	7/8/2015 6:31	56	8/8/2015 23:36	57
3/8/2015 2:16	57	4/8/2015 3:21	56	5/8/2015 4:26	57	6/8/2015 5:31	57	7/8/2015 6:36	57	8/8/2015 23:41	57
3/8/2015 2:21	57	4/8/2015 3:26	56	5/8/2015 4:31	56	6/8/2015 5:36	57	7/8/2015 6:41	56	8/8/2015 23:46	59
3/8/2015 2:26	56	4/8/2015 3:31	56	5/8/2015 4:36	56	6/8/2015 5:41	58	7/8/2015 6:46	58	8/8/2015 23:51	57
3/8/2015 2:31	56	4/8/2015 3:36	57	5/8/2015 4:41	56	6/8/2015 5:46	58	7/8/2015 6:51	59	8/8/2015 23:56	56
3/8/2015 2:36	55	4/8/2015 3:41	56	5/8/2015 4:46	56	6/8/2015 5:51	58	7/8/2015 6:56	59	9/8/2015 0:01	56
3/8/2015 2:41	56	4/8/2015 3:46	56	5/8/2015 4:51	56	6/8/2015 5:56	57	7/8/2015 23:01	58	9/8/2015 0:06	57
3/8/2015 2:46	56	4/8/2015 3:51	57	5/8/2015 4:56	57	6/8/2015 6:01	45	7/8/2015 23:06	59	9/8/2015 0:11	57
3/8/2015 2:51	56	4/8/2015 3:56	56	5/8/2015 5:01	57	6/8/2015 6:06	49	7/8/2015 23:11	58	9/8/2015 0:16	57
3/8/2015 2:56	57	4/8/2015 4:01	56	5/8/2015 5:06	57	6/8/2015 6:11	54	7/8/2015 23:16	59	9/8/2015 0:21	57
3/8/2015 3:01	57	4/8/2015 4:06	56	5/8/2015 5:11	57	6/8/2015 6:16	53	7/8/2015 23:21	60	9/8/2015 0:26	56
3/8/2015 3:06	56	4/8/2015 4:11	57	5/8/2015 5:16	56	6/8/2015 6:21	57	7/8/2015 23:26	59	9/8/2015 0:31	56
3/8/2015 3:11	55	4/8/2015 4:16	56	5/8/2015 5:21	56	6/8/2015 6:26	55	7/8/2015 23:31	58	9/8/2015 0:36	56
3/8/2015 3:16	57	4/8/2015 4:21	56	5/8/2015 5:26	57	6/8/2015 6:31	56	7/8/2015 23:36	58	9/8/2015 0:41	60
3/8/2015 3:21	57	4/8/2015 4:26	57	5/8/2015 5:31	57	6/8/2015 6:36	55	7/8/2015 23:41	59	9/8/2015 0:46	53
3/8/2015 3:26	56	4/8/2015 4:31	56	5/8/2015 5:36	57	6/8/2015 6:41	58	7/8/2015 23:46	57	9/8/2015 0:51	54
3/8/2015 3:31	56	4/8/2015 4:36	57	5/8/2015 5:41	58	6/8/2015 6:46	58	7/8/2015 23:51	57	9/8/2015 0:56	56
3/8/2015 3:36	56	4/8/2015 4:41	55	5/8/2015 5:46	58	6/8/2015 6:51	58	7/8/2015 23:56	57	9/8/2015 1:01	56
3/8/2015 3:41	56	4/8/2015 4:46	56	5/8/2015 5:51	46	6/8/2015 6:56	59	8/8/2015 0:01	5		


Real-time Noise Data		RTN2a (Hong Kong Electric Centre)									
9/8/2015 3:41	58	10/8/2015 4:46	58	11/8/2015 5:51	51	12/8/2015 6:56	59	14/8/2015 0:01	58	15/8/2015 1:06	56
9/8/2015 3:46	58	10/8/2015 4:51	57	11/8/2015 5:56	52	12/8/2015 23:01	58	14/8/2015 0:06	57	15/8/2015 1:11	55
9/8/2015 3:51	58	10/8/2015 4:56	58	11/8/2015 6:01	51	12/8/2015 23:06	58	14/8/2015 0:11	54	15/8/2015 1:16	52
9/8/2015 3:56	58	10/8/2015 5:01	57	11/8/2015 6:06	52	12/8/2015 23:11	57	14/8/2015 0:16	56	15/8/2015 1:21	53
9/8/2015 4:01	58	10/8/2015 5:06	58	11/8/2015 6:11	54	12/8/2015 23:16	58	14/8/2015 0:21	56	15/8/2015 1:26	54
9/8/2015 4:06	58	10/8/2015 5:11	57	11/8/2015 6:16	55	12/8/2015 23:21	57	14/8/2015 0:26	56	15/8/2015 1:31	56
9/8/2015 4:11	51	10/8/2015 5:16	58	11/8/2015 6:21	57	12/8/2015 23:26	59	14/8/2015 0:31	59	15/8/2015 1:36	54
9/8/2015 4:16	58	10/8/2015 5:21	58	11/8/2015 6:26	58	12/8/2015 23:31	57	14/8/2015 0:36	68	15/8/2015 1:41	54
9/8/2015 4:21	58	10/8/2015 5:26	45	11/8/2015 6:31	58	12/8/2015 23:36	56	14/8/2015 0:41	67	15/8/2015 1:46	53
9/8/2015 4:26	58	10/8/2015 5:31	58	11/8/2015 6:36	57	12/8/2015 23:41	57	14/8/2015 0:46	56	15/8/2015 1:51	56
9/8/2015 4:31	58	10/8/2015 5:36	57	11/8/2015 6:41	62	12/8/2015 23:46	56	14/8/2015 0:51	59	15/8/2015 1:56	55
9/8/2015 4:36	44	10/8/2015 5:41	58	11/8/2015 6:46	64	12/8/2015 23:51	58	14/8/2015 0:56	57	15/8/2015 2:01	55
9/8/2015 4:41	58	10/8/2015 5:46	58	11/8/2015 6:51	61	12/8/2015 23:56	58	14/8/2015 1:01	56	15/8/2015 2:06	53
9/8/2015 4:46	38	10/8/2015 5:51	49	11/8/2015 6:56	61	13/8/2015 0:01	53	14/8/2015 1:06	54	15/8/2015 2:11	51
9/8/2015 4:51	58	10/8/2015 5:56	52	11/8/2015 23:01	64	13/8/2015 0:06	53	14/8/2015 1:11	56	15/8/2015 2:16	51
9/8/2015 4:56	58	10/8/2015 6:01	50	11/8/2015 23:06	58	13/8/2015 0:11	54	14/8/2015 1:16	52	15/8/2015 2:21	52
9/8/2015 5:01	45	10/8/2015 6:06	52	11/8/2015 23:11	57	13/8/2015 0:16	54	14/8/2015 1:21	53	15/8/2015 2:26	53
9/8/2015 5:06	58	10/8/2015 6:11	54	11/8/2015 23:16	58	13/8/2015 0:21	56	14/8/2015 1:26	55	15/8/2015 2:31	54
9/8/2015 5:11	58	10/8/2015 6:16	57	11/8/2015 23:21	57	13/8/2015 0:26	52	14/8/2015 1:31	52	15/8/2015 2:36	52
9/8/2015 5:16	57	10/8/2015 6:21	56	11/8/2015 23:26	57	13/8/2015 0:31	57	14/8/2015 1:36	55	15/8/2015 2:41	52
9/8/2015 5:21	58	10/8/2015 6:26	57	11/8/2015 23:31	57	13/8/2015 0:36	54	14/8/2015 1:41	54	15/8/2015 2:46	55
9/8/2015 5:26	58	10/8/2015 6:31	58	11/8/2015 23:36	57	13/8/2015 0:41	54	14/8/2015 1:46	50	15/8/2015 2:51	51
9/8/2015 5:31	32	10/8/2015 6:36	58	11/8/2015 23:41	56	13/8/2015 0:46	54	14/8/2015 1:51	37	15/8/2015 2:56	50
9/8/2015 5:36	40	10/8/2015 6:41	59	11/8/2015 23:46	55	13/8/2015 0:51	51	14/8/2015 1:56	54	15/8/2015 3:01	40
9/8/2015 5:41	58	10/8/2015 6:46	60	11/8/2015 23:51	56	13/8/2015 0:56	50	14/8/2015 2:01	55	15/8/2015 3:06	49
9/8/2015 5:46	58	10/8/2015 6:51	60	11/8/2015 23:56	55	13/8/2015 1:01	55	14/8/2015 2:06	53	15/8/2015 3:11	46
9/8/2015 5:51	50	10/8/2015 6:56	60	12/8/2015 0:01	54	13/8/2015 1:06	47	14/8/2015 2:11	45	15/8/2015 3:16	51
9/8/2015 5:56	58	10/8/2015 23:01	57	12/8/2015 0:06	56	13/8/2015 1:11	43	14/8/2015 2:16	52	15/8/2015 3:21	58
9/8/2015 6:01	49	10/8/2015 23:06	57	12/8/2015 0:11	55	13/8/2015 1:16	48	14/8/2015 2:21	52	15/8/2015 3:26	58
9/8/2015 6:06	52	10/8/2015 23:11	58	12/8/2015 0:16	56	13/8/2015 1:21	47	14/8/2015 2:26	53	15/8/2015 3:31	45
9/8/2015 6:11	52	10/8/2015 23:16	57	12/8/2015 0:21	53	13/8/2015 1:26	46	14/8/2015 2:31	57	15/8/2015 3:36	58
9/8/2015 6:16	50	10/8/2015 23:21	57	12/8/2015 0:26	55	13/8/2015 1:31	47	14/8/2015 2:36	58	15/8/2015 3:41	58
9/8/2015 6:21	49	10/8/2015 23:26	57	12/8/2015 0:31	55	13/8/2015 1:36	53	14/8/2015 2:41	45	15/8/2015 3:46	58
9/8/2015 6:26	54	10/8/2015 23:31	56	12/8/2015 0:36	55	13/8/2015 1:41	49	14/8/2015 2:46	62	15/8/2015 3:51	58
9/8/2015 6:31	55	10/8/2015 23:36	56	12/8/2015 0:41	54	13/8/2015 1:46	58	14/8/2015 2:51	63	15/8/2015 3:56	58
9/8/2015 6:36	53	10/8/2015 23:41	56	12/8/2015 0:46	55	13/8/2015 1:51	38	14/8/2015 2:56	59	15/8/2015 4:01	58
9/8/2015 6:41	55	10/8/2015 23:46	56	12/8/2015 0:51	56	13/8/2015 1:56	58	14/8/2015 3:01	62	15/8/2015 4:06	43
9/8/2015 6:46	55	10/8/2015 23:51	55	12/8/2015 0:56	49	13/8/2015 2:01	58	14/8/2015 3:06	67	15/8/2015 4:11	58
9/8/2015 6:51	56	10/8/2015 23:56	56	12/8/2015 1:01	51	13/8/2015 2:06	57	14/8/2015 3:11	55	15/8/2015 4:16	58
9/8/2015 6:56	55	11/8/2015 0:01	55	12/8/2015 1:06	44	13/8/2015 2:11	57	14/8/2015 3:16	50	15/8/2015 4:21	57
9/8/2015 23:01	59	11/8/2015 0:06	53	12/8/2015 1:11	52	13/8/2015 2:16	57	14/8/2015 3:21	61	15/8/2015 4:26	57
9/8/2015 23:06	58	11/8/2015 0:11	51	12/8/2015 1:16	49	13/8/2015 2:21	56	14/8/2015 3:26	51	15/8/2015 4:31	58
9/8/2015 23:11	58	11/8/2015 0:16	56	12/8/2015 1:21	50	13/8/2015 2:26	58	14/8/2015 3:31	48	15/8/2015 4:36	57
9/8/2015 23:16	58	11/8/2015 0:21	53	12/8/2015 1:26	51	13/8/2015 2:31	58	14/8/2015 3:36	58	15/8/2015 4:41	57
9/8/2015 23:21	59	11/8/2015 0:26	52	12/8/2015 1:31	42	13/8/2015 2:36	57	14/8/2015 3:41	58	15/8/2015 4:46	58
9/8/2015 23:26	57	11/8/2015 0:31	55	12/8/2015 1:36	58	13/8/2015 2:41	57	14/8/2015 3:46	58	15/8/2015 4:51	57
9/8/2015 23:31	58	11/8/2015 0:36	52	12/8/2015 1:41	44	13/8/2015 2:46	57	14/8/2015 3:51	58	15/8/2015 4:56	57
9/8/2015 23:36	58	11/8/2015 0:41	51	12/8/2015 1:46	58	13/8/2015 2:51	57	14/8/2015 3:56	54	15/8/2015 5:01	44
9/8/2015 23:41	57	11/8/2015 0:46	51	12/8/2015 1:51	58	13/8/2015 2:56	57	14/8/2015 4:01	54	15/8/2015 5:06	57
9/8/2015 23:46	57	11/8/2015 0:51	50	12/8/2015 1:56	58	13/8/2015 3:01	57	14/8/2015 4:06	58	15/8/2015 5:11	48
9/8/2015 23:51	55	11/8/2015 0:56	57	12/8/2015 2:01	57	13/8/2015 3:06	56	14/8/2015 4:11	58	15/8/2015 5:16	57
9/8/2015 23:56	56	11/8/2015 1:01	59	12/8/2015 2:06	58	13/8/2015 3:11	57	14/8/2015 4:16	58	15/8/2015 5:21	58
10/8/2015 0:01	56	11/8/2015 1:06	53	12/8/2015 2:11	57	13/8/2015 3:16	57	14/8/2015 4:21	58	15/8/2015 5:26	58
10/8/2015 0:06	56	11/8/2015 1:11	53	12/8/2015 2:16	58	13/8/2015 3:21	56	14/8/2015 4:26	57	15/8/2015 5:31	58
10/8/2015 0:11	56	11/8/2015 1:16	47	12/8/2015 2:21	57	13/8/2015 3:26	57	14/8/2015 4:31	58	15/8/2015 5:36	58
10/8/2015 0:16	55	11/8/2015 1:21	51	12/8/2015 2:26	57	13/8/2015 3:31	57	14/8/2015 4:36	58	15/8/2015 5:41	58
10/8/2015 0:21	56	11/8/2015 1:26	44	12/8/2015 2:31	57	13/8/2015 3:36	57	14/8/2015 4:41	58	15/8/2015 5:46	42
10/8/2015 0:26	55	11/8/2015 1:31	49	12/8/2015 2:36	58	13/8/2015 3:41	57	14/8/2015 4:46	58	15/8/2015 5:51	49
10/8/2015 0:31	53	11/8/2015 1:36	58	12/8/2015 2:41	57	13/8/2015 3:46	57	14/8/2015 4:51	58	15/8/2015 5:56	45
10/8/2015 0:36	49	11/8/2015 1:41	58	12/8/2015 2:46	58	13/8/2015 3:51	57	14/8/2015 4:56	57	15/8/2015 6:01	58
10/8/2015 0:41	52	11/8/2015 1:46	57	12/8/2015 2:51	57	13/8/2015 3:56	56	14/8/2015 5:01	58	15/8/2015 6:06	51
10/8/2015 0:46	51	11/8/2015 1:51	58	12/8/2015 2:56	50	13/8/2015 4:01	56	14/8/2015 5:06	58	15/8/2015 6:11	54
10/8/2015 0:51	50	11/8/2015 1:56	58	12/8/2015 3:01	56	13/8/2015 4:06	57	14/8/2015 5:11	58	15/8/2015 6:16	60
10/8/2015 0:56	54	11/8/2015 2:01	58	12/8/2015 3:06	57	13/8/2015 4:11	57	14/8/2015 5:16	42	15/8/2015 6:21	62
10/8/2015 1:01	54	11/8/2015 2:06	61	12/8/2015 3:11	57	13/8/2015 4:16	56	14/8/2015 5:21	58	15/8/2015 6:26	58
10/8/2015 1:06	55	11/8/2015 2:11	58	12/8/2015 3:16	57	13/8/2015 4:21	56	14/8/2015 5:26	58	15/8/2015 6:31	60
10/8/2015 1:11	55	11/8/2015 2:16	42	12/8/2015 3:21	56	13/8/2015 4:26	56	14/8/2015 5:31	58	15/8/2015 6:36	60
10/8/2015 1:16	56	11/8/2015 2:21	53	12/8/2015 3:26	57	13/8/2015 4:31	56	14/8/2015 5:36	47	15/8/2015 6:41	57
10/8/2015 1:21	66	11/8/2015 2:26	57	12/8/2015 3:31	56	13/8/2015 4:36	56	14/8/2015 5:41	46	15/8/2015 6:46	58
10/8/2015 1:26	70	11/8/2015 2:31	57	12/8/2015 3:36	56	13/8/2015 4:41	56	14/8/2015 5:46	64	15/8/2015 6:51	60
10/8/2015 1:31	68	11/8/2015 2:36	57	12/8/2015 3:41	57	13/8/2015 4:46	56	14/8/2015 5:51	62	15/8/2015 6:56	59
10/8/2015 1:36	64	11/8/2015 2:41	57	12/8/2015 3:46	56	13/8/2015 4:51	57	14/8/2015 5:56	57	15/8/2015 23:01	59
10/8/2015 1:41	59	11/8/2015 2:46	58	12/8/2015 3:51	56	13/8/2015 4:56	56	14/8/2015 6:01	53	15/8/2015 23:06	58
10/8/2015 1:46	54	11/8/2015 2:51	58	12/8/2015 3:56	56	13/8/2015 5:01	57	14/8/2015 6:06	51	15/8/2015 23:11	58
10/8/2015 1:51	50	11/8/2015 2:56	57	12/8/2015 4:01	56	13/8/2015 5:06	57	14/8/2015 6:11	53	15/8/2015 23:16	60
10/8/2015 1:56	52	11/8/2015 3:01	58	12/8/2015 4:06	57	13/8/2015 5:11	58	14/8/2015 6:16	57	15/8/2015 23:21	58
10/8/2015 2:01	45	11									

Real-time Noise Data	RTN2a (Hong Kong Electric Centre)										
16/8/2015 2:11	38	17/8/2015 3:16	57	18/8/2015 4:21	57	19/8/2015 5:26	57	20/8/2015 6:31	57	21/8/2015 23:36	62
16/8/2015 2:16	44	17/8/2015 3:21	56	18/8/2015 4:26	57	19/8/2015 5:31	58	20/8/2015 6:36	57	21/8/2015 23:41	58
16/8/2015 2:21	58	17/8/2015 3:26	56	18/8/2015 4:31	56	19/8/2015 5:36	57	20/8/2015 6:41	57	21/8/2015 23:46	56
16/8/2015 2:26	48	17/8/2015 3:31	56	18/8/2015 4:36	56	19/8/2015 5:41	58	20/8/2015 6:46	59	21/8/2015 23:51	56
16/8/2015 2:31	52	17/8/2015 3:36	56	18/8/2015 4:41	57	19/8/2015 5:46	44	20/8/2015 6:51	60	21/8/2015 23:56	58
16/8/2015 2:36	43	17/8/2015 3:41	56	18/8/2015 4:46	57	19/8/2015 5:51	58	20/8/2015 6:56	59	22/8/2015 0:01	56
16/8/2015 2:41	47	17/8/2015 3:46	56	18/8/2015 4:51	57	19/8/2015 5:56	49	20/8/2015 23:01	59	22/8/2015 0:06	57
16/8/2015 2:46	38	17/8/2015 3:51	56	18/8/2015 4:56	56	19/8/2015 6:01	59	20/8/2015 23:06	58	22/8/2015 0:11	57
16/8/2015 2:51	58	17/8/2015 3:56	57	18/8/2015 5:01	57	19/8/2015 6:06	52	20/8/2015 23:11	58	22/8/2015 0:16	56
16/8/2015 2:56	37	17/8/2015 4:01	56	18/8/2015 5:06	57	19/8/2015 6:11	52	20/8/2015 23:16	57	22/8/2015 0:21	56
16/8/2015 3:01	47	17/8/2015 4:06	56	18/8/2015 5:11	57	19/8/2015 6:16	52	20/8/2015 23:21	59	22/8/2015 0:26	57
16/8/2015 3:06	57	17/8/2015 4:11	57	18/8/2015 5:16	56	19/8/2015 6:21	56	20/8/2015 23:26	58	22/8/2015 0:31	55
16/8/2015 3:11	51	17/8/2015 4:16	57	18/8/2015 5:21	57	19/8/2015 6:26	56	20/8/2015 23:31	57	22/8/2015 0:36	56
16/8/2015 3:16	50	17/8/2015 4:21	57	18/8/2015 5:26	57	19/8/2015 6:31	56	20/8/2015 23:36	58	22/8/2015 0:41	57
16/8/2015 3:21	44	17/8/2015 4:26	57	18/8/2015 5:31	58	19/8/2015 6:36	58	20/8/2015 23:41	58	22/8/2015 0:46	56
16/8/2015 3:26	58	17/8/2015 4:31	56	18/8/2015 5:36	58	19/8/2015 6:41	59	20/8/2015 23:46	58	22/8/2015 0:51	55
16/8/2015 3:31	58	17/8/2015 4:36	57	18/8/2015 5:41	58	19/8/2015 6:46	58	20/8/2015 23:51	56	22/8/2015 0:56	57
16/8/2015 3:36	42	17/8/2015 4:41	56	18/8/2015 5:46	58	19/8/2015 6:51	59	20/8/2015 23:56	56	22/8/2015 1:01	54
16/8/2015 3:41	58	17/8/2015 4:46	56	18/8/2015 5:51	57	19/8/2015 6:56	60	21/8/2015 0:01	57	22/8/2015 1:06	54
16/8/2015 3:46	58	17/8/2015 4:51	57	18/8/2015 5:56	35	19/8/2015 23:01	58	21/8/2015 0:06	57	22/8/2015 1:11	55
16/8/2015 3:51	58	17/8/2015 4:56	56	18/8/2015 6:01	47	19/8/2015 23:06	58	21/8/2015 0:11	57	22/8/2015 1:16	55
16/8/2015 3:56	58	17/8/2015 5:01	56	18/8/2015 6:06	49	19/8/2015 23:11	56	21/8/2015 0:16	56	22/8/2015 1:21	55
16/8/2015 4:01	58	17/8/2015 5:06	57	18/8/2015 6:11	53	19/8/2015 23:16	59	21/8/2015 0:21	56	22/8/2015 1:26	55
16/8/2015 4:06	57	17/8/2015 5:11	57	18/8/2015 6:16	53	19/8/2015 23:21	56	21/8/2015 0:26	57	22/8/2015 1:31	53
16/8/2015 4:11	58	17/8/2015 5:16	54	18/8/2015 6:21	55	19/8/2015 23:26	56	21/8/2015 0:31	56	22/8/2015 1:36	55
16/8/2015 4:16	58	17/8/2015 5:21	57	18/8/2015 6:26	54	19/8/2015 23:31	57	21/8/2015 0:36	57	22/8/2015 1:41	54
16/8/2015 4:21	58	17/8/2015 5:26	57	18/8/2015 6:31	56	19/8/2015 23:36	56	21/8/2015 0:41	54	22/8/2015 1:46	54
16/8/2015 4:26	58	17/8/2015 5:31	57	18/8/2015 6:36	57	19/8/2015 23:41	56	21/8/2015 0:46	52	22/8/2015 1:51	54
16/8/2015 4:31	58	17/8/2015 5:36	58	18/8/2015 6:41	59	19/8/2015 23:46	55	21/8/2015 0:51	52	22/8/2015 1:56	52
16/8/2015 4:36	58	17/8/2015 5:41	58	18/8/2015 6:46	58	19/8/2015 23:51	55	21/8/2015 0:56	52	22/8/2015 2:01	53
16/8/2015 4:41	58	17/8/2015 5:46	58	18/8/2015 6:51	59	19/8/2015 23:56	55	21/8/2015 1:01	52	22/8/2015 2:06	53
16/8/2015 4:46	57	17/8/2015 5:51	48	18/8/2015 6:56	60	20/8/2015 0:01	55	21/8/2015 1:06	51	22/8/2015 2:11	52
16/8/2015 4:51	58	17/8/2015 5:56	58	18/8/2015 23:01	60	20/8/2015 0:06	53	21/8/2015 1:11	50	22/8/2015 2:16	51
16/8/2015 4:56	58	17/8/2015 6:01	32	18/8/2015 23:06	57	20/8/2015 0:11	55	21/8/2015 1:16	58	22/8/2015 2:21	50
16/8/2015 5:01	40	17/8/2015 6:06	48	18/8/2015 23:11	58	20/8/2015 0:16	52	21/8/2015 1:21	49	22/8/2015 2:26	54
16/8/2015 5:06	57	17/8/2015 6:11	54	18/8/2015 23:16	58	20/8/2015 0:21	56	21/8/2015 1:26	51	22/8/2015 2:31	50
16/8/2015 5:11	58	17/8/2015 6:16	54	18/8/2015 23:21	57	20/8/2015 0:26	55	21/8/2015 1:31	50	22/8/2015 2:36	44
16/8/2015 5:16	58	17/8/2015 6:21	55	18/8/2015 23:26	57	20/8/2015 0:31	53	21/8/2015 1:36	46	22/8/2015 2:41	58
16/8/2015 5:21	57	17/8/2015 6:26	55	18/8/2015 23:31	56	20/8/2015 0:36	48	21/8/2015 1:41	43	22/8/2015 2:46	49
16/8/2015 5:26	58	17/8/2015 6:31	57	18/8/2015 23:36	55	20/8/2015 0:41	52	21/8/2015 1:46	43	22/8/2015 2:51	45
16/8/2015 5:31	58	17/8/2015 6:36	55	18/8/2015 23:41	55	20/8/2015 0:46	53	21/8/2015 1:51	47	22/8/2015 2:56	32
16/8/2015 5:36	58	17/8/2015 6:41	58	18/8/2015 23:46	55	20/8/2015 0:51	52	21/8/2015 1:56	52	22/8/2015 3:01	58
16/8/2015 5:41	57	17/8/2015 6:46	60	18/8/2015 23:51	55	20/8/2015 0:56	58	21/8/2015 2:01	54	22/8/2015 3:06	45
16/8/2015 5:46	58	17/8/2015 6:51	60	18/8/2015 23:56	55	20/8/2015 1:01	50	21/8/2015 2:06	38	22/8/2015 3:11	58
16/8/2015 5:51	58	17/8/2015 6:56	59	19/8/2015 0:01	55	20/8/2015 1:06	57	21/8/2015 2:11	58	22/8/2015 3:16	58
16/8/2015 5:56	49	17/8/2015 23:01	61	19/8/2015 0:06	55	20/8/2015 1:11	50	21/8/2015 2:16	57	22/8/2015 3:21	58
16/8/2015 6:01	58	17/8/2015 23:06	59	19/8/2015 0:11	55	20/8/2015 1:16	58	21/8/2015 2:21	57	22/8/2015 3:26	58
16/8/2015 6:06	58	17/8/2015 23:11	59	19/8/2015 0:16	53	20/8/2015 1:21	52	21/8/2015 2:26	58	22/8/2015 3:31	38
16/8/2015 6:11	45	17/8/2015 23:16	58	19/8/2015 0:21	54	20/8/2015 1:26	47	21/8/2015 2:31	57	22/8/2015 3:36	43
16/8/2015 6:16	58	17/8/2015 23:21	59	19/8/2015 0:26	51	20/8/2015 1:31	51	21/8/2015 2:36	57	22/8/2015 3:41	48
16/8/2015 6:21	46	17/8/2015 23:26	58	19/8/2015 0:31	54	20/8/2015 1:36	57	21/8/2015 2:41	57	22/8/2015 3:46	45
16/8/2015 6:26	52	17/8/2015 23:31	57	19/8/2015 0:36	54	20/8/2015 1:41	32	21/8/2015 2:46	57	22/8/2015 3:51	58
16/8/2015 6:31	53	17/8/2015 23:36	57	19/8/2015 0:41	47	20/8/2015 1:46	58	21/8/2015 2:51	58	22/8/2015 3:56	58
16/8/2015 6:36	53	17/8/2015 23:41	57	19/8/2015 0:46	54	20/8/2015 1:51	57	21/8/2015 2:56	57	22/8/2015 4:01	58
16/8/2015 6:41	55	17/8/2015 23:46	55	19/8/2015 0:51	53	20/8/2015 1:56	57	21/8/2015 3:01	57	22/8/2015 4:06	58
16/8/2015 6:46	55	17/8/2015 23:51	56	19/8/2015 0:56	52	20/8/2015 2:01	58	21/8/2015 3:06	57	22/8/2015 4:11	58
16/8/2015 6:51	56	17/8/2015 23:56	56	19/8/2015 1:01	49	20/8/2015 2:06	57	21/8/2015 3:11	56	22/8/2015 4:16	46
16/8/2015 6:56	56	18/8/2015 0:01	57	19/8/2015 1:06	58	20/8/2015 2:11	56	21/8/2015 3:16	57	22/8/2015 4:21	58
16/8/2015 23:01	59	18/8/2015 0:06	55	19/8/2015 1:11	46	20/8/2015 2:16	57	21/8/2015 3:21	58	22/8/2015 4:26	58
16/8/2015 23:06	57	18/8/2015 0:11	56	19/8/2015 1:16	58	20/8/2015 2:21	57	21/8/2015 3:26	57	22/8/2015 4:31	58
16/8/2015 23:11	56	18/8/2015 0:16	54	19/8/2015 1:21	58	20/8/2015 2:26	57	21/8/2015 3:31	57	22/8/2015 4:36	57
16/8/2015 23:16	56	18/8/2015 0:21	54	19/8/2015 1:26	47	20/8/2015 2:31	57	21/8/2015 3:36	57	22/8/2015 4:41	58
16/8/2015 23:21	55	18/8/2015 0:26	55	19/8/2015 1:31	58	20/8/2015 2:36	57	21/8/2015 3:41	58	22/8/2015 4:46	58
16/8/2015 23:26	56	18/8/2015 0:31	53	19/8/2015 1:36	58	20/8/2015 2:41	57	21/8/2015 3:46	57	22/8/2015 4:51	58
16/8/2015 23:31	56	18/8/2015 0:36	53	19/8/2015 1:41	58	20/8/2015 2:46	57	21/8/2015 3:51	56	22/8/2015 4:56	58
16/8/2015 23:36	55	18/8/2015 0:41	46	19/8/2015 1:46	58	20/8/2015 2:51	57	21/8/2015 3:56	57	22/8/2015 5:01	58
16/8/2015 23:41	56	18/8/2015 0:46	50	19/8/2015 1:51	58	20/8/2015 2:56	58	21/8/2015 4:01	56	22/8/2015 5:06	58
16/8/2015 23:46	56	18/8/2015 0:51	50	19/8/2015 1:56	50	20/8/2015 3:01	58	21/8/2015 4:06	56	22/8/2015 5:11	38
16/8/2015 23:51	55	18/8/2015 0:56	49	19/8/2015 2:01	58	20/8/2015 3:06	57	21/8/2015 4:11	58	22/8/2015 5:16	58
16/8/2015 23:56	54	18/8/2015 1:01	47	19/8/2015 2:06	58	20/8/2015 3:11	56	21/8/2015 4:16	57	22/8/2015 5:21	49
17/8/2015 0:01	54	18/8/2015 1:06	58	19/8/2015 2:11	58	20/8/2015 3:16	57	21/8/2015 4:21	57	22/8/2015 5:26	57
17/8/2015 0:06	52	18/8/2015 1:11	32	19/8/2015 2:16	58	20/8/2015 3:21	57	21/8/2015 4:26	57	22/8/2015 5:31	58
17/8/2015 0:11	52	18/8/2015 1:16	47	19/8/2015 2:21	58	20/8/2015 3:26	57	21/8/2015 4:31	56	22/8/2015 5:36	58
17/8/2015 0:16	52	18/8/2015 1:21	47	19/8/2015 2:26	58	20/8/2015 3:31	57	21/8/2015 4:36	57	22/8/2015 5:41	47
17/8/2015 0:21	54	18/8/2015 1:26	45	19/8/2015 2:31	57	20/8/2015 3:36	57	21/8/2015 4:41	57	22/8/2015 5:46	47
17/8/2015 0:26	54	18/8/2015 1:31	58	19/8/2015 2:36	57	20/8/2015 3:41	56	21/8/2015 4:46	57	22/	

Real-time Noise Data		RTN2a (Hong Kong Electric Centre)					
23/8/2015 0:41	53	24/8/2015 1:46	57	25/8/2015 2:51	46	26/8/2015 3:56	57
23/8/2015 0:46	55	24/8/2015 1:51	57	25/8/2015 2:56	56	26/8/2015 4:01	56
23/8/2015 0:51	52	24/8/2015 1:56	57	25/8/2015 3:01	57	26/8/2015 4:06	56
23/8/2015 0:56	52	24/8/2015 2:01	58	25/8/2015 3:06	57	26/8/2015 4:11	56
23/8/2015 1:01	52	24/8/2015 2:06	57	25/8/2015 3:11	57	26/8/2015 4:16	57
23/8/2015 1:06	54	24/8/2015 2:11	57	25/8/2015 3:16	58	26/8/2015 4:21	57
23/8/2015 1:11	51	24/8/2015 2:16	57	25/8/2015 3:21	58	26/8/2015 4:26	58
23/8/2015 1:16	49	24/8/2015 2:21	57	25/8/2015 3:26	58	26/8/2015 4:31	57
23/8/2015 1:21	52	24/8/2015 2:26	57	25/8/2015 3:31	57	26/8/2015 4:36	57
23/8/2015 1:26	52	24/8/2015 2:31	50	25/8/2015 3:36	57	26/8/2015 4:41	57
23/8/2015 1:31	53	24/8/2015 2:36	57	25/8/2015 3:41	58	26/8/2015 4:46	57
23/8/2015 1:36	50	24/8/2015 2:41	57	25/8/2015 3:46	57	26/8/2015 4:51	56
23/8/2015 1:41	54	24/8/2015 2:46	57	25/8/2015 3:51	57	26/8/2015 4:56	56
23/8/2015 1:46	47	24/8/2015 2:51	56	25/8/2015 3:56	57	26/8/2015 5:01	56
23/8/2015 1:51	40	24/8/2015 2:56	56	25/8/2015 4:01	56	26/8/2015 5:06	57
23/8/2015 1:56	48	24/8/2015 3:01	56	25/8/2015 4:06	56	26/8/2015 5:11	57
23/8/2015 2:01	58	24/8/2015 3:06	56	25/8/2015 4:11	57	26/8/2015 5:16	58
23/8/2015 2:06	58	24/8/2015 3:11	56	25/8/2015 4:16	57	26/8/2015 5:21	58
23/8/2015 2:11	49	24/8/2015 3:16	56	25/8/2015 4:21	56	26/8/2015 5:26	57
23/8/2015 2:16	58	24/8/2015 3:21	55	25/8/2015 4:26	56	26/8/2015 5:31	58
23/8/2015 2:21	54	24/8/2015 3:26	56	25/8/2015 4:31	57	26/8/2015 5:36	58
23/8/2015 2:26	58	24/8/2015 3:31	56	25/8/2015 4:36	57	26/8/2015 5:41	57
23/8/2015 2:31	47	24/8/2015 3:36	56	25/8/2015 4:41	57	26/8/2015 5:46	58
23/8/2015 2:36	46	24/8/2015 3:41	56	25/8/2015 4:46	58	26/8/2015 5:51	58
23/8/2015 2:41	58	24/8/2015 3:46	56	25/8/2015 4:51	58	26/8/2015 5:56	48
23/8/2015 2:46	58	24/8/2015 3:51	57	25/8/2015 4:56	57	26/8/2015 6:01	58
23/8/2015 2:51	58	24/8/2015 3:56	56	25/8/2015 5:01	57	26/8/2015 6:06	46
23/8/2015 2:56	58	24/8/2015 4:01	56	25/8/2015 5:06	57	26/8/2015 6:11	41
23/8/2015 3:01	45	24/8/2015 4:06	56	25/8/2015 5:11	57	26/8/2015 6:16	52
23/8/2015 3:06	58	24/8/2015 4:11	56	25/8/2015 5:16	57	26/8/2015 6:21	55
23/8/2015 3:11	57	24/8/2015 4:16	56	25/8/2015 5:21	57	26/8/2015 6:26	55
23/8/2015 3:16	57	24/8/2015 4:21	57	25/8/2015 5:26	58	26/8/2015 6:31	55
23/8/2015 3:21	58	24/8/2015 4:26	57	25/8/2015 5:31	58	26/8/2015 6:36	55
23/8/2015 3:26	58	24/8/2015 4:31	56	25/8/2015 5:36	58	26/8/2015 6:41	58
23/8/2015 3:31	58	24/8/2015 4:36	57	25/8/2015 5:41	58	26/8/2015 6:46	57
23/8/2015 3:36	57	24/8/2015 4:41	57	25/8/2015 5:46	58	26/8/2015 6:51	57
23/8/2015 3:41	58	24/8/2015 4:46	56	25/8/2015 5:51	46	26/8/2015 6:56	59
23/8/2015 3:46	58	24/8/2015 4:51	56	25/8/2015 5:56	58	26/8/2015 23:01	57
23/8/2015 3:51	56	24/8/2015 4:56	56	25/8/2015 6:01	58	26/8/2015 23:06	58
23/8/2015 3:56	57	24/8/2015 5:01	56	25/8/2015 6:06	51	26/8/2015 23:11	56
23/8/2015 4:01	62	24/8/2015 5:06	57	25/8/2015 6:11	53	26/8/2015 23:16	57
23/8/2015 4:06	57	24/8/2015 5:11	56	25/8/2015 6:16	52	26/8/2015 23:21	59
23/8/2015 4:11	57	24/8/2015 5:16	57	25/8/2015 6:21	55	26/8/2015 23:26	57
23/8/2015 4:16	57	24/8/2015 5:21	57	25/8/2015 6:26	55	26/8/2015 23:31	55
23/8/2015 4:21	57	24/8/2015 5:26	57	25/8/2015 6:31	56	26/8/2015 23:36	57
23/8/2015 4:26	56	24/8/2015 5:31	57	25/8/2015 6:36	57	26/8/2015 23:41	57
23/8/2015 4:31	57	24/8/2015 5:36	58	25/8/2015 6:41	57	26/8/2015 23:46	56
23/8/2015 4:36	57	24/8/2015 5:41	58	25/8/2015 6:46	58	26/8/2015 23:51	56
23/8/2015 4:41	57	24/8/2015 5:46	41	25/8/2015 6:51	58	26/8/2015 23:56	55
23/8/2015 4:46	57	24/8/2015 5:51	58	25/8/2015 6:56	59	27/8/2015 0:01	56
23/8/2015 4:51	58	24/8/2015 5:56	49	25/8/2015 23:01	57	27/8/2015 0:06	57
23/8/2015 4:56	57	24/8/2015 6:01	58	25/8/2015 23:06	58	27/8/2015 0:11	57
23/8/2015 5:01	57	24/8/2015 6:06	58	25/8/2015 23:11	57	27/8/2015 0:16	55
23/8/2015 5:06	57	24/8/2015 6:11	50	25/8/2015 23:16	57	27/8/2015 0:21	55
23/8/2015 5:11	58	24/8/2015 6:16	55	25/8/2015 23:21	58	27/8/2015 0:26	53
23/8/2015 5:16	57	24/8/2015 6:21	55	25/8/2015 23:26	57	27/8/2015 0:31	54
23/8/2015 5:21	58	24/8/2015 6:26	55	25/8/2015 23:31	57	27/8/2015 0:36	52
23/8/2015 5:26	57	24/8/2015 6:31	61	25/8/2015 23:36	57	27/8/2015 0:41	55
23/8/2015 5:31	58	24/8/2015 6:36	58	25/8/2015 23:41	55	27/8/2015 0:46	46
23/8/2015 5:36	58	24/8/2015 6:41	59	25/8/2015 23:46	56	27/8/2015 0:51	51
23/8/2015 5:41	58	24/8/2015 6:46	59	25/8/2015 23:51	56	27/8/2015 0:56	42
23/8/2015 5:46	58	24/8/2015 6:51	60	25/8/2015 23:56	55	27/8/2015 1:01	58
23/8/2015 5:51	58	24/8/2015 6:56	59	26/8/2015 0:01	55	27/8/2015 1:06	50
23/8/2015 5:56	58	24/8/2015 23:01	56	26/8/2015 0:06	56	27/8/2015 1:11	43
23/8/2015 6:01	58	24/8/2015 23:06	58	26/8/2015 0:11	52	27/8/2015 1:16	58
23/8/2015 6:06	55	24/8/2015 23:11	56	26/8/2015 0:16	51	27/8/2015 1:21	58
23/8/2015 6:11	48	24/8/2015 23:16	57	26/8/2015 0:21	53	27/8/2015 1:26	53
23/8/2015 6:16	47	24/8/2015 23:21	58	26/8/2015 0:26	52	27/8/2015 1:31	52
23/8/2015 6:21	55	24/8/2015 23:26	56	26/8/2015 0:31	50	27/8/2015 1:36	52
23/8/2015 6:26	54	24/8/2015 23:31	55	26/8/2015 0:36	52	27/8/2015 1:41	47
23/8/2015 6:31	53	24/8/2015 23:36	56	26/8/2015 0:41	50	27/8/2015 1:46	49
23/8/2015 6:36	53	24/8/2015 23:41	56	26/8/2015 0:46	52	27/8/2015 1:51	52
23/8/2015 6:41	57	24/8/2015 23:46	55	26/8/2015 0:51	49	27/8/2015 1:56	51
23/8/2015 6:46	55	24/8/2015 23:51	55	26/8/2015 0:56	48	27/8/2015 2:01	57
23/8/2015 6:51	57	24/8/2015 23:56	54	26/8/2015 1:01	49	27/8/2015 2:06	58
23/8/2015 6:56	59	25/8/2015 0:01	56	26/8/2015 1:06	49	27/8/2015 2:11	58
23/8/2015 23:01	57	25/8/2015 0:06	54	26/8/2015 1:11	54	27/8/2015 2:16	57
23/8/2015 23:06	56	25/8/2015 0:11	52	26/8/2015 1:16	44	27/8/2015 2:21	57
23/8/2015 23:11	57	25/8/2015 0:16	55	26/8/2015 1:21	46	27/8/2015 2:26	58
23/8/2015 23:16	57	25/8/2015 0:21	53	26/8/2015 1:26	58	27/8/2015 2:31	57
23/8/2015 23:21	57	25/8/2015 0:26	54	26/8/2015 1:31	48	27/8/2015 2:36	57
23/8/2015 23:26	56	25/8/2015 0:31	54	26/8/2015 1:36	58	27/8/2015 2:41	58
23/8/2015 23:31	53	25/8/2015 0:36	51	26/8/2015 1:41	58	27/8/2015 2:46	58
23/8/2015 23:36	55	25/8/2015 0:41	52	26/8/2015 1:46	58	27/8/2015 2:51	58
23/8/2015 23:41	53	25/8/2015 0:46	49	26/8/2015 1:51	57	27/8/2015 2:56	57
23/8/2015 23:46	62	25/8/2015 0:51	43	26/8/2015 1:56	57	27/8/2015 3:01	57
23/8/2015 23:51	57	25/8/2015 0:56	44	26/8/2015 2:01	58	27/8/2015 3:06	57
23/8/2015 23:56	57	25/8/2015 1:01	49	26/8/2015 2:06	57	27/8/2015 3:11	57
24/8/2015 0:01	51	25/8/2015 1:06	53	26/8/2015 2:11	57	27/8/2015 3:16	57
24/8/2015 0:06	55	25/8/2015 1:11	51	26/8/2015 2:16	57	27/8/2015 3:21	56
24/8/2015 0:11	54	25/8/2015 1:16	46	26/8/2015 2:21	56	27/8/2015 3:26	56
24/8/2015 0:16	54	25/8/2015 1:21	49	26/8/2015 2:26	57	27/8/2015 3:31	57
24/8/2015 0:21	52	25/8/2015 1:26	42	26/8/2015 2:31	57	27/8/2015 3:36	56
24/8/2015 0:26	52	25/8/2015 1:31	60	26/8/2015 2:36	58	27/8/2015 3:41	57
24/8/2015 0:31	49	25/8/2015 1:36	55	26/8/2015 2:41	57	27/8/2015 3:46	57
24/8/2015 0:36	50	25/8/2015 1:41	52	26/8/2015 2:46	58	27/8/2015 3:51	57
24/8/2015 0:41	58	25/8/2015 1:46	58	26/8/2015 2:51	57	27/8/2015 3:56	57
24/8/2015 0:46	32	25/8/2015 1:51	58	26/8/2015 2:56	57	27/8/2015 4:01	57
24/8/2015 0:51	47	25/8/2015 1:56	42	26/8/2015 3:01	57	27/8/2015 4:06	57
24/8/2015 0:56	58	25/8/2015 2:01	61	26/8/2015 3:06	58	27/8/2015 4:11	57
24/8/2015 1:01	58	25/8/2015 2:06	58	26/8/2015 3:11	57	27/8/2015 4:16	56
24/8/2015 1:06	46	25/8/2015 2:11	57	26/8/2015 3:16	56	27/8/2015 4:21	57
24/8/2015 1:11	58	25/8/2015 2:16	58	26/8/2015 3:21	57	27/8/2015 4:26	56
24/8/2015 1:16	47	25/8/2015 2:21	57	26/8/2015 3:26	56	27/8/2015 4:31	57
24/8/2015 1:21	43	25/8/2015 2:26	58	26/8/2015 3:31	57	27/8/2015 4:36	57
24/8/2015 1:26	58	25/8/2015 2:31	58	26/8/2015 3:36	57	27/8/2015 4:41	57
24/8/2015 1:31	32	25/8/2015 2:36	58	26/8/2015 3:41	58	27/8/2015 4:46	56
24/8/2015 1:36	38	25/8/2015 2:41	58	26/8/2015 3:46	56	27/8/2015 4:51	57
24/8/2015 1:41	58	25/8/2015 2:46	57	26/8/2015 3:51	57	27/8/2015 4:56	55



Graphic Presentation of Real Time Noise Monitoring Result (RTN2a- Hong Kong Electric Centre)

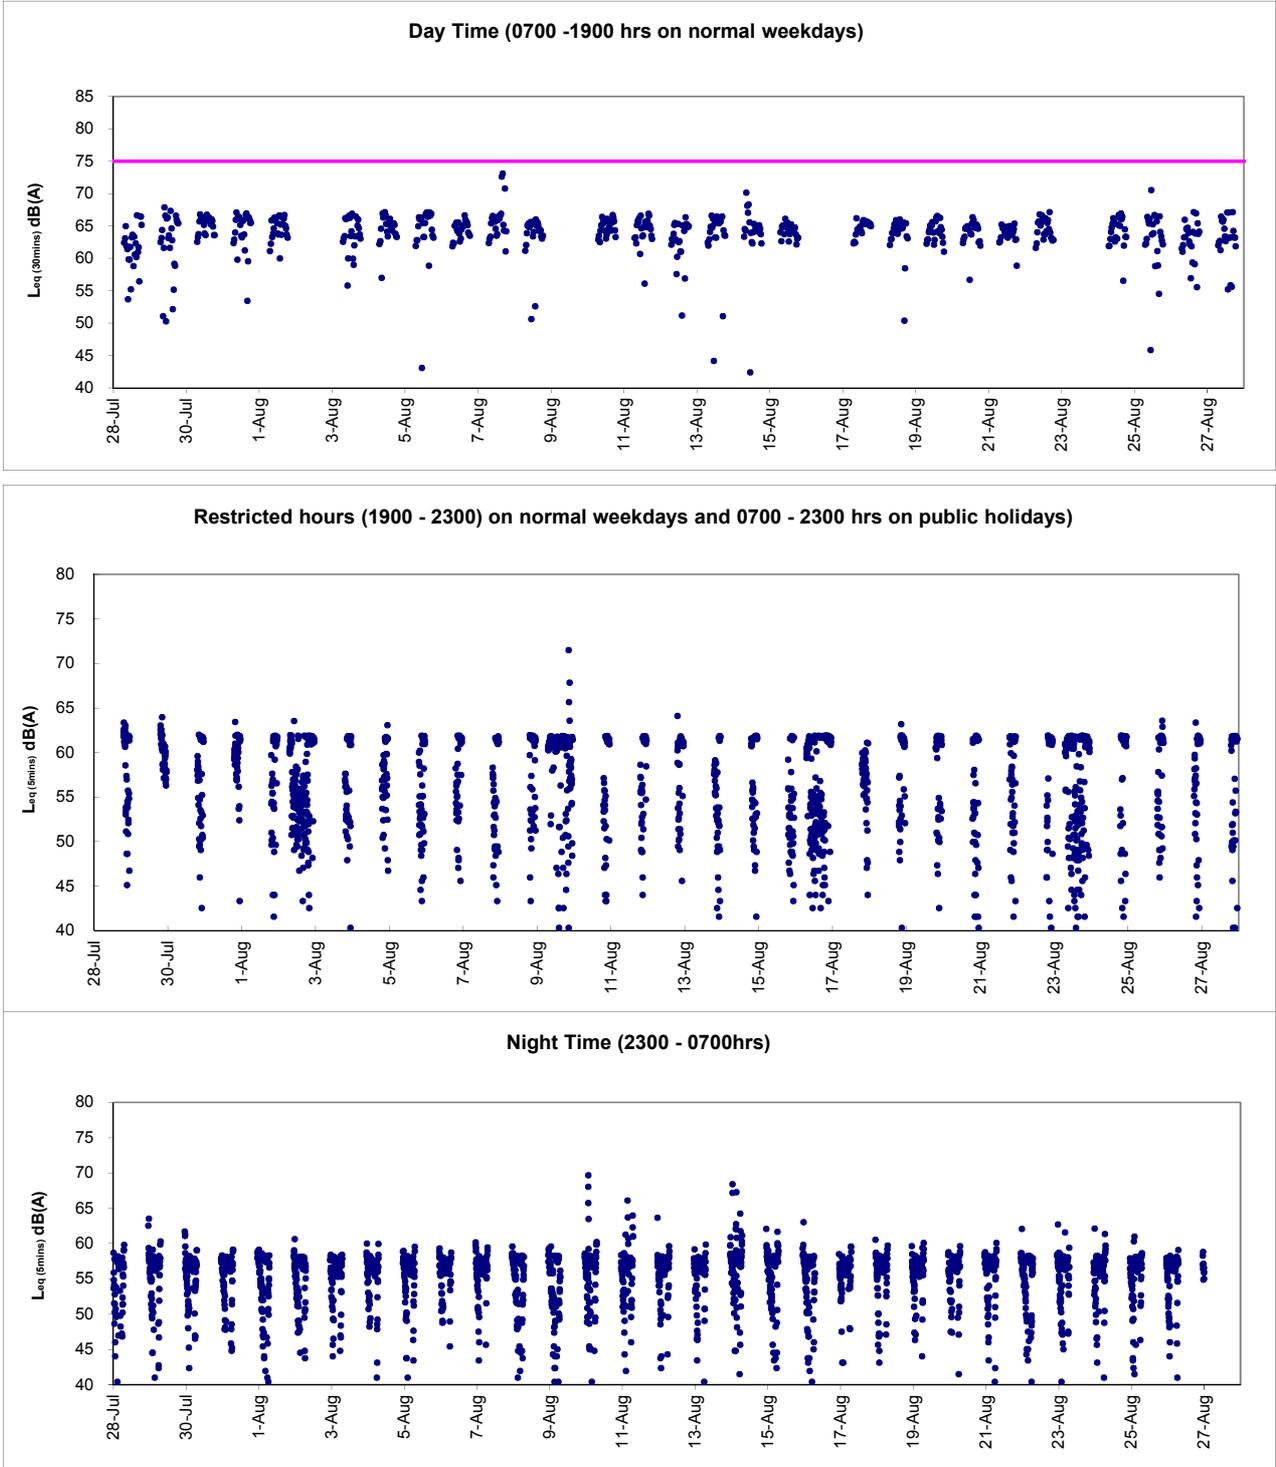



***Appendix 6.1***

***Event Action Plans***



Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded	<ol style="list-style-type: none"><li>1. Notify ER, IEC and Contractor;</li><li>2. Carry out investigation;</li><li>3. Report the results of investigation to the IEC, ER and Contractor;</li><li>4. Discuss with the IEC and Contractor on remedial measures required;</li><li>5. Increase monitoring frequency to check mitigation effectiveness.</li></ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"><li>1. Review the investigation results submitted by the ET;</li><li>2. Review the proposed remedial measures by the Contractor and advise the ER accordingly;</li><li>3. Advise the ER on the effectiveness of the proposed remedial measures.</li></ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"><li>1. Confirm receipt of notification of failure in writing;</li><li>2. Notify Contractor;</li><li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li><li>4. Supervise the implementation of remedial measures.</li></ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>	<ol style="list-style-type: none"><li>1. Submit noise mitigation proposals to IEC and ER;</li><li>2. Implement noise mitigation proposals.</li></ol> <p>(The above actions should be taken within 2 working days after the exceedance is identified)</p>



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit Level being exceeded	<ol style="list-style-type: none"> <li>1. Inform IEC, ER, Contractor and EPD;</li> <li>2. Repeat measurements to confirm findings;</li> <li>3. Increase monitoring frequency;</li> <li>4. Identify source and investigate the cause of exceedance;</li> <li>5. Carry out analysis of Contractor's working procedures;</li> <li>6. Discuss with the IEC, Contractor and ER on remedial measures required;</li> <li>7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>8. If exceedance stops, cease additional monitoring. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol style="list-style-type: none"> <li>1. Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol style="list-style-type: none"> <li>1. Confirm receipt of notification of failure in writing;</li> <li>2. Notify Contractor;</li> <li>3. In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>4. Supervise the implementation of remedial measures;</li> <li>5. If exceedance continues, consider stopping the Contractor to continue working on that portion of work which causes the exceedance until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>	<ol style="list-style-type: none"> <li>1. Take immediate action to avoid further exceedance;</li> <li>2. Submit proposals for remedial actions to IEC and ER within 3 working days of notification;</li> <li>3. Implement the agreed proposals;</li> <li>4. Submit further proposal if problem still not under control;</li> <li>5. Stop the relevant portion of works as instructed by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>



**Event / Action Plan for Construction Air Quality**

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
<b>ACTION LEVEL</b>				
1. Exceedance for one sample	<ol style="list-style-type: none"> <li>Identify source, investigate the causes of exceedance and propose remedial measures; Inform IEC and ER;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Notify Contractor.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Rectify any unacceptable practice;</li> <li>Amend working methods if appropriate.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>Identify source;</li> <li>Inform IEC and ER;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Repeat measurements to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Discuss with IEC and Contractor on remedial actions required;</li> <li>If exceedance continues, arrange meeting with IEC and ER;</li> <li>If exceedance stops, cease additional monitoring.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ET on the effectiveness of the proposed remedial measures;</li> <li>Supervise Implementation of remedial measures.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Ensure remedial measures properly implemented.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Submit proposals for remedial to ER within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)
<b>LIMIT LEVEL</b>				
1. Exceedance for one sample	<ol style="list-style-type: none"> <li>Identify source, investigate the causes of exceedance and propose remedial measures; Inform ER, Contractor and EPD;</li> <li>Repeat measurement to confirm finding;</li> <li>Increase monitoring frequency to daily;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Check monitoring data submitted by ET;</li> <li>Check Contractor's working method;</li> <li>Discuss with ET and Contractor on possible remedial measures;</li> <li>Advise the ER on the effectiveness of the proposed remedial measures;</li> <li>Supervise implementation of remedial measures.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>Ensure remedial measures properly implemented.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Amend proposal if appropriate.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> <li>Notify IEC, ER, Contractor and EPD;</li> <li>Identify source;</li> <li>Repeat measurement to confirm findings;</li> <li>Increase monitoring frequency to daily;</li> <li>Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented;</li> <li>Arrange meeting with IEC and ER to discuss the remedial actions to be taken;</li> <li>Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</li> <li>If exceedance stops, cease additional monitoring.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Discuss amongst ER, ET, and Contractor on the potential remedial actions;</li> <li>Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly;</li> <li>Supervise the implementation of remedial measures.</li> </ol>	<ol style="list-style-type: none"> <li>Confirm receipt of notification of failure in writing;</li> <li>Notify Contractor;</li> <li>In consolidation with the IEC, agree with the Contractor on the remedial measures to be implemented;</li> <li>Ensure remedial measures properly implemented;</li> <li>If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</li> </ol> (The above actions should be taken within 2 working days after the exceedance is identified)	<ol style="list-style-type: none"> <li>Take immediate action to avoid further exceedance;</li> <li>Submit proposals for remedial actions to IEC within 3 working days of notification;</li> <li>Implement the agreed proposals;</li> <li>Resubmit proposals if problem still not under control;</li> <li>Stop the relevant portion of works as determined by the ER until the exceedance is abated. (The above actions should be taken within 2 working days after the exceedance is identified)</li> </ol>



**Event and Action Plan for Marine Water Quality**

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level being exceeded by one sampling day	Repeat in-situ measurement to confirm findings; Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)
Action level being exceeded by more than one consecutive sampling days	Identify source(s) of impact; Inform IEC and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IEC and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; (The above actions should be taken within 1 working day after the exceedance is identified) Repeat measurement on next working day of exceedance.	Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Discuss with IEC on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)	Inform the Engineer and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; Implement the agreed mitigation measures. (The above actions should be taken within 1 working day after the exceedance is identified)



EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Limit level being exceeded by one sampling day	<p>Repeat in-situ measurement to confirm findings;            Identify source(s) of impact; Inform IEC, contractor and EPD;            Check monitoring data, all plant, equipment and Contractor's working methods;            Discuss mitigation measures with IEC, ER and Contractor; Ensure mitigation measures are implemented;            Increase the monitoring frequency to daily until no exceedance of Limit level.            (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Discuss with ET and Contractor on the mitigation measures;            Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly;            Assess the effectiveness of the implemented mitigation measures.            (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Discuss with IEC, ET and Contractor on the proposed mitigation measures;            Request Contractor to critically review the working methods;            Make agreement on the mitigation measures to be implemented;            Assess the effectiveness of the implemented mitigation measures.            (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Inform the Engineer and confirm notification of the non-compliance in writing;            Rectify unacceptable practice;            Check all plant and equipment;            Consider changes of working methods;            Discuss with ET , IEC and ER and propose mitigation measures to IEC and ER within 3 working days;            Implement the agreed mitigation measures.            (The above actions should be taken within 1 working day after the exceedance is identified)</p>
Limit level being exceeded by more than one consecutive sampling days	<p>Identify source(s) of impact; Inform IEC, contractor and EPD;            Check monitoring data, all plant, equipment and Contractor's working methods;            Discuss mitigation measures with IEC, ER and Contractor;            Ensure mitigation measures are implemented;            Increase the monitoring frequency to daily until no exceedance of Limit level for two consecutive days.            (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Discuss with ET and Contractor on the mitigation measures;            Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly;            Assess the effectiveness of the implemented mitigation measures.            (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Discuss with IEC, ET and Contractor on the proposed mitigation measures;            Request Contractor to critically review the working methods;            Make agreement on the mitigation measures to be implemented;            Assess the effectiveness of the implemented mitigation measures;            Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit level.            (The above actions should be taken within 1 working day after the exceedance is identified)</p>	<p>Inform the ER and confirm notification of the non-compliance in writing;            Rectify unacceptable practice;            Check all plant and equipment;            Consider changes of working methods;            Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3working days;            Implement the agreed mitigation measures;            As directed by the Engineer, to slow down or to stop all or part of the marine work or construction activities.            (The above actions should be taken within 1 working day after the exceedance is identified)</p>



**Event and Action Plan for Odour Patrol**

Event	ACTION	
	Person-in-charge of Odour Monitoring	Implementation Agent Identified by CEDD
<b>Action Level</b>		
Exceedance of Action Level	1. Identify source/reason of exceedance; 2. Repeat odour patrol to confirm finding.	1. Carry out investigation to identify the source/reason of exceedance; 2. Rectify any unacceptable practice 3. Implement more mitigation measures if necessary; 4. Inform EPD or MD if exceedance is considered to be caused by expedient connections or floating debris.
<b>Limit Level</b>		
Exceedance of Limit Level	1. Identify source / reason of exceedance; 2. Repeat odour patrol to confirm findings; 3. Increase odour patrol frequency; 4. If exceedance stops, cease additional odour patrol.	1. Carry out investigation to identify the source/reason of exceedance. Investigation shall be completed within 2 weeks; 2. Rectify any unacceptable practice; 3. Formulate remedial actions; 4. Ensure remedial actions properly implemented; 5. If exceedance continues, consider what more/enhanced mitigation measures shall be implemented; 6. Inform EPD or MD if exceedance is considered to be caused by expedient connections or floating debris.



***Appendix 6.2***

***Summary for Notification of Exceedance***



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_15A018	27-Aug-15	9:56	CMA2a - Causeway Bay Community Bay	380.9	1hr TSP (ug/m <sup>3</sup> )	323.4	500	<p><b>Possible reason:</b> Elevated TSP level in relate to the external wall renovation undertaken at Causeway Bay Community Centre by non-CWB Project Contractors.</p> <p><b>Action taken / to be taken:</b> Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures.</p> <p><b>Remarks / Other Obs:</b> In view of IEC bridge deck lifting with crane around Watson road with no considerable dust impact was undertaken by the Contractor of HY/2009/19 on the monitoring date while external wall renovation including tile removal using hand held breaker was undertaken by non-CWB Contractor at Causeway Bay Community Centre and considered as the major source of dust impact during monitoring, the exceedance was considered not related to the Project.</p>
X_15A019	27-Aug-15	14:00	CMA2a - Causeway Bay Community Bay	350.1	1hr TSP (ug/m <sup>3</sup> )	323.4	500	<p><b>Possible reason:</b> Elevated TSP level in relate to the external wall renovation undertaken at Causeway Bay Community Centre by non-CWB Project Contractors.</p> <p><b>Action taken / to be taken:</b> Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures.</p> <p><b>Remarks / Other Obs:</b> In view of IEC bridge deck lifting with crane around Watson road with no considerable dust impact was undertaken by the Contractor of HY/2009/19 on the monitoring date while external wall renovation including tile removal using hand held breaker was undertaken by non-CWB Contractor at Causeway Bay Community Centre and considered as the major source of dust impact during monitoring, the exceedance was considered not related to the Project.</p>



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_15A020	27-Aug-15	9:56	CMA2a - Causeway Bay Community Bay	380.9	1hr TSP (ug/m <sup>3</sup> )	323.4	500	<p><b>Possible reason:</b> Elevated TSP level in relate to the external wall renovation undertaken at Causeway Bay Community Centre by non-CWB Project Contractors.</p> <p><b>Action taken / to be taken:</b> Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures.</p> <p><b>Remarks / Other Obs:</b> In view of wall/ ceiling washing within a section tunnel area outside Watson with considerable dust impact was undertaken by the Contract of HY/2011/08 on the monitoring date while external wall renovation including tile removal using hand held breaker was undertaken by non-CWB Contractor at Causeway Bay Community Centre and considered as the major source of dust impact during monitoring, the exceedance was considered not related to the Project.</p>
X_15A021	27-Aug-15	14:00	CMA2a - Causeway Bay Community Bay	350.1	1hr TSP (ug/m <sup>3</sup> )	323.4	500	<p><b>Possible reason:</b> Elevated TSP level in relate to the external wall renovation undertaken at Causeway Bay Community Centre by non-CWB Project Contractors.</p> <p><b>Action taken / to be taken:</b> Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures.</p> <p><b>Remarks / Other Obs:</b> In view of wall/ ceiling washing within a section tunnel area outside Watson with considerable dust impact was undertaken by the Contract of HY/2011/08 on the monitoring date while external wall renovation including tile removal using hand held breaker was undertaken by non-CWB Contractor at Causeway Bay Community Centre and considered as the major source of dust impact during monitoring, the exceedance was considered not related to the Project.</p>



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_15A016	26-Aug-15	8:00	CMA2a - Causeway Bay Community Bay	218.3	24hr TSP (ug/m <sup>3</sup> )	169.5	260	<p><b>Possible reason:</b> Elevated TSP level in relate to the external wall renovation undertaken at Causeway Bay Community Centre by non-CWB Project Contractors.</p> <p><b>Action taken / to be taken:</b> Reviewed the trend of air quality measurement across monitoring stations. Analysis of Contractor's working procedures.</p> <p><b>Remarks / Other Obs:</b> Although IEC bridge deck saw cutting and wire cutting were undertaken on the monitoring date at around Watson Road under Contractor of HY/2009/19, mitigation measure including watering during cutting works was generally implemented. According to the observation on the monitoring date, external wall renovation including tile removal using hand held breaker was undertaken by non-CWB Contractor at Causeway Bay Community Centre and considered as the major source of dust impact during monitoring. As such, the exceedance was considered not related to the Project.</p>



Ref. No.	Date	Time	Location	Measured TSP Level	Unit	Action Level	Limit Level	Follow-up action
X_15A017	26-Aug-15	8:00	CMA2a - Causeway Bay Community Bay	218.3	24hr TSP (ug/m <sup>3</sup> )	169.5	260	<p><b>Possible reason:</b> Elevated TSP level in relate to the external wall renovation undertaken at Causeway Bay Community Centre by non-CWB Project Contractors.</p> <p><b>Action taken / to be taken:</b> Reviewed the trend of air quality measurement across monitoring stations. Analysis of contractor's working procedures.</p> <p><b>Remarks / Other Obs:</b> In view of wall/ ceiling washing within a section tunnel area outside Watson with no considerable dust impact was conducted under the Contract of HY/2011/08 on the monitoring date while external wall renovation including tile removal using hand held breaker was undertaken by non-CWB Contractor at Causeway Bay Community Centre and considered as the major source of dust impact during monitoring, the exceedance was considered not related to the Project.</p>



Ref no.	Date	Tidal	Location	Depth	Parameters (Unit)	Measured	Action Level	Limit Level	Follow-up action
X_10D522	3-Aug-15	Mid-ebb	Ex-WPCWA SW	Middle	DO(mg/l)	1.85	3.19	3.10	<p><b>Possible reason:</b> Possible in relation to the upstream organic discharge.</p> <p><b>Action taken/ to be taken:</b> Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.</p> <p><b>Remarks/ Other Obs:</b> Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted and no exceedance was recorded on the subsequent monitoring, the exceedance was considered not related to the Project works. DO level was restored to normal level above WQO on 5 August 2015 during flood tide.</p>
X_10D523	5-Aug-15	Mid-ebb	Ex-WPCWA SW	Middle	DO(mg/l)	2.78	3.19	3.10	<p><b>Possible reason:</b> Possible in relation to the upstream organic discharge.</p> <p><b>Action taken/ to be taken:</b> Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.</p> <p><b>Remarks/ Other Obs:</b> Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted and no exceedance was recorded on the subsequent monitoring, the exceedance was considered not related to the Project works.</p>
X_10D524	14-Aug-15	Mid-ebb	Ex-WPCWA SE	Middle	DO(mg/l)	3.54	3.55	3.00	<p><b>Possible reason:</b> Possible in relation to the upstream organic discharge.</p> <p><b>Action taken/ to be taken:</b> Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.</p> <p><b>Remarks/ Other Obs:</b> Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order provided while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted and no exceedance was recorded on the subsequent monitoring, the exceedance was considered not related to the Project works.</p>
X_10D525	14-Aug-15	Mid-flood	Ex-WPCWA SW	Middle	DO(mg/l)	2.98	3.19	3.10	<p><b>Possible reason:</b> Possible in relation to the upstream organic discharge.</p> <p><b>Action taken/ to be taken:</b> Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.</p> <p><b>Remarks/ Other Obs:</b> Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted and no exceedance was recorded on the subsequent monitoring, the exceedance was considered not related to the Project works.</p>



Ref no.	Date	Tidal	Location	Depth	Parameters (Unit)	Measured	Action Level	Limit Level	Follow-up action
X_10D526	17-Aug-15	Mid-ebb	Ex-WPCWA SW	Middle	DO(mg/l)	2.59	3.19	3.10	<p><b>Possible reason:</b> Possible in relation to the upstream organic discharge.</p> <p><b>Action taken/ to be taken:</b> Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.</p> <p><b>Remarks/ Other Obs:</b> Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted, the exceedance was considered not related to the Project works. The DO level at the concerned location was subsequently resumed on 21 August 2015 flood tide.</p>
X_10D527	17-Aug-15	Mid-ebb	Ex-WPCWA SE	Middle	DO(mg/l)	2.51	3.55	3.00	<p><b>Possible reason:</b> Possible in relation to the upstream organic discharge.</p> <p><b>Action taken/ to be taken:</b> Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.</p> <p><b>Remarks/ Other Obs:</b> Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted, the exceedance was considered not related to the Project works. Nevertheless, the contractor was reminded to increase the frequency of floating refuses collection and reposition floating curtain to eliminate any potential effect to the water quality within the area. The DO level at the concerned location was subsequently resumed on 21 August 2015 flood tide.</p>
X_10D528	19-Aug-15	Mid-flood	Ex-WPCWA SE	Middle	DO(mg/l)	3.02	3.55	3.00	<p><b>Possible reason:</b> Possible in relation to the upstream organic discharge.</p> <p><b>Action taken/ to be taken:</b> Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.</p> <p><b>Remarks/ Other Obs:</b> Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted, the exceedance was considered not related to the Project works. Nevertheless, the contractor was reminded to increase the frequency of floating refuses collection and reposition floating curtain to eliminate any potential effect to the water quality within the area. The DO level at the concerned location was subsequently resumed on 21 August 2015 flood tide.</p>
X_10D529	19-Aug-15	Mid-ebb	Ex-WPCWA SE	Middle	DO(mg/l)	3.30	3.55	3.00	<p><b>Possible reason:</b> Possible in relation to the upstream organic discharge.</p> <p><b>Action taken/ to be taken:</b> Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.</p> <p><b>Remarks/ Other Obs:</b> Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted and no exceedance was recorded on the subsequent monitoring, the exceedance was considered not related to the Project works.</p>



Ref no.	Date	Tidal	Location	Depth	Parameters (Unit)	Measured	Action Level	Limit Level	Follow-up action	
X_10D530	19-Aug-15	Mid-ebb	Ex-WPCWA SW	Middle	DO(mg/l)	2.87	3.19	3.10	<p><b>Possible reason:</b></p>	Possible in relation to the upstream organic discharge.
									<p><b>Action taken/ to be taken:</b></p>	Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.
									<p><b>Remarks/ Other Obs:</b></p>	Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted and no exceedance was recorded on the subsequent monitoring, the exceedance was considered not related to the Project works.
X_10D531	27-Aug-15	Mid-ebb	Ex-WPCWA SW	Middle	DO(mg/l)	2.83	3.19	3.10	<p><b>Possible reason:</b></p>	Possible in relation to the upstream organic discharge.
									<p><b>Action taken/ to be taken:</b></p>	Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.
									<p><b>Remarks/ Other Obs:</b></p>	Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted and no exceedance was recorded on the subsequent monitoring, the exceedance was considered not related to the Project works.
X_10D532	27-Aug-15	Mid-flood	Ex-WPCWA SE	Middle	DO(mg/l)	3.30	3.55	3.00	<p><b>Possible reason:</b></p>	Possible in relation to the upstream organic discharge.
									<p><b>Action taken/ to be taken:</b></p>	Repeated the measurement to confirm the result. No odour nuisance was noted during the DO monitoring. Checking with contractor works and review previous monitoring data.
									<p><b>Remarks/ Other Obs:</b></p>	Despite excavated mud transshipment was conducted at Ex-WPCWA on the monitoring date, the construction works conducted was generally in order while upstream discharge from nearby culvert were consistently observed. In view of no dredging or reclamation works activity was conducted, the exceedance was considered not related to the Project works.



***Appendix 9.1***

***Complaint Log***

**Environmental Complaints Log**

Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
100321a	21/3/2010	ICC Case no. 1-224618029, Ms. Tsang	Location near Tin Hau	Complaint regarding the loud noise and dark smoke in the course of dredging works on 21 March 2010 (Sunday).	<ol style="list-style-type: none"><li>1) A valid Construction Noise Permit no. GW-RS0119-10 was granted from EPD since 18<sup>th</sup> Feb. 2010 for the dredging works which carry out at area for North Point Reclamation.</li><li>2) Officer from Marine Department, Police and EPD's officer attended the scene for inspection and investigation.</li><li>3) The Contractor (CHEC-CRBC JV) strictly comply all the conditions in CNP and take all mitigation measures in order to minimize the potential impacts to surrounding sensitive receivers. A formal letter was issued out by CHEC-CRBC JV and to explain the status of the recent construction activities.</li><li>4) No limit level exceedance was recorded on the noise measurement during day time and evening time noise measurement on 23 March 2010. Additional restrict hours noise monitoring at Causeway Bay Community and City Garden was conducted on 5 April 2010 (Public Holiday). No limit level exceedance was recorded in the monitoring.</li><li>5) No further complaints were received from Mr. Tsang in the reporting month. The complaint is considered closed.</li></ol>	Closed
100321b	21/3/2010	Unknown	Near the eastern breakwater of the Causeway Bay Typhoon Shelter	A public complaint and enquiry regarding loud noises emanated from dredging activities on 21/3/2010 (Sunday) until 2220 hours and between 1920-1946 hours in the evening of 22 March 2010(Monday).	<ol style="list-style-type: none"><li>1) A valid Construction Noise Permit no. GW-RS0119-10 was granted from EPD since 18<sup>th</sup> Feb. 2010 for the dredging works at area for North Point Reclamation during general holidays including Sunday between 0700-2300 hours and any day not being a general holiday between 1900-2300hours. It is complied with the condition of CNP.</li><li>2) Officer from Marine Department, Police and EPD's officer attended the scene for inspection and investigation.</li><li>3) No limit level exceedance was recorded on the noise measurement during day time and evening time noise measurement on 23 March 2010. Additional restrict hours noise monitoring at Causeway Bay Community and City Garden was conducted on 5 April 2010 (Public Holiday). No limit level exceedance was recorded in the monitoring.</li><li>4) No further complaints were received in the reporting month. The complaint is considered closed.</li></ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
100504	4/5/2010	Public complainant received by ICC (ICC case: 1-233384048)	Watson Road	Complaint on the noise nuisance due to the large scale of dredging machine (face to Island East Corridor) in particular the hours 1900 to 0800 and request to reduce the noise level.	<ol style="list-style-type: none"><li>1) Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0119-10 for their dredging works. Contractor has implemented mitigation measures to reduce the working hour not later than 2230.</li><li>2) According to RSS 's record, no more daytime and night time dredging since the departure of the split hopper barge from the workplace on 29 April 2010 at 1900 hrs to 5 May 2010.</li><li>3) No further complaints were received in the reporting month. The complaint is considered closed.</li></ol>	Closed
100731	31/7/2010	Mr. Lee received by ICC (CC Case: 1-250702681)	Oil Street to Watson Road	Complaint on the noise nuisance due to the dredging works. Three construction plants were operated concurrently.	<ol style="list-style-type: none"><li>1) Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0371-10 for their dredging works.</li><li>2) There was only 1 grab dredger operated by Contractor within NPR project site area for dredging works.</li><li>3) No noise exceedance was recorded at noise monitoring station at Victoria Centre on 27 July and 3 August 2010 during daytime and evening time period.</li><li>4) It is considered as invalid from the EP and CNP point of view.</li></ol>	Closed
100812	12/8/2010	Mr. Wong, Harbour Heights (Management) Ltd.	Harbour Heights	Management office received their resident complained on the noise nuisance from the dredging works at the marine works area adjacent to the Harbour Height during the period from 0700 to 2200.	<ol style="list-style-type: none"><li>1) Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0371-10 for their dredging works. Contractor has implemented mitigation measures to reduce the working hour not later than 2230.</li><li>2) No noise exceedance was recorded at noise monitoring station at Victoria Centre on 10 and 17 August 2010 during daytime and evening time period.</li><li>3) It is considered as invalid complaint. No further complaints were received in the reporting month. The complaint is considered closed.</li></ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
101108	8/11/2010	Mr. Nip received by ICC (CC Case)	Sai Wan Ho	Visual concern around the seaside silt screen outside the WSD freshwater intake pump at Sai Wan Ho (Monitoring station ref no.. WSD15)	<ol style="list-style-type: none"><li>1) Contractor for HY/2009/11 has been regular checked of condition and removal of trapped rubbish before the dismantling of the floating silt screen to be replaced by wall mount silt screen.</li><li>2) Follow-up action had been immediately carried out to check and clear the floating refuse around the seaside silt screen after receipt of the complaint.</li><li>3) Removal of seaside silt screen outside the WSD freshwater intake (WSD15) by contractor HY/2009/11 was checked and confirmed dated 9 November 2010. Silt screen has been deployed into the existing steel frame at WSD15 for the protection of WSD salt water intake.</li></ol>	Closed
101110	10/11/2010	Mr. Wong, Harbour Heights (Management) Ltd.	Harbour Heights	Management office received their resident complained on the noise nuisance from the power mechanical equipment during the 0700 to 2200hrs	<ol style="list-style-type: none"><li>1) Contractor for HY/2009/11 was granted valid Construction Noise Permit no. GW-RS0870-10 for their dredging works during evening time. Contractor has implemented mitigation measures to reduce the working hour not later than 2230.</li><li>2) No noise exceedance was recorded at noise monitoring station at Victoria Centre on 4 and 10 November 2010 during daytime and evening time period.</li><li>3) It is considered as invalid complaint. No further complaints were received in the reporting month. The complaint is considered closed.</li></ol>	Closed
101203	3/12/2010, 01:45a.m.	The resident of Block 11, City Garden by ICC referral from Marine Department	North Point	Bad odour was generated from the dredging plant off North Point	<ol style="list-style-type: none"><li>1) The first investigation was carried out by Marine Department patrol in the morning on 3 Dec 2010 at around 10:00 and revealed that a few working barges were anchoring in the vicinity without carrying out dredging work.</li><li>2) A further specific investigation inspection on contractor's backhoe barge in the vicinity of City Garden was jointly conducted with Engineer Representatives (AECOM/RSS), and ET on 8 Dec 2010 at 11:30. No bad odour was noted during the investigation.</li><li>3) Routine dredging operation of the backhoe barge was performed during the jointed investigation inspection and it was revealed that no bad odour was attributed by the dredged materials inspected.</li></ol>	Closed
101206	6/12/2010	Ms Lui, the resident of 27/F, Block 10, City	City Garden, North Point	Two barges were generating noise at 22:00 on 6 December 2010 in which the noise from	<ol style="list-style-type: none"><li>1) ET confirmed the following information with resident site staff on the complaint:<ul style="list-style-type: none"><li>• It was referred to the filling operation at North Point</li></ul></li></ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		Garden by ICC (ICC case: 1-266039336)		<p>filling operation was louder than the traffic noise &amp; visual impact was generated due to the spot-light pointing directly to the complainant flat, suspected the filling operation was part of Wanchai Development Phase II;</p> <p>Complainant also raised the same complaint to District Councillor, Mr. Hui on 7 Dec 2010 regarding the night-time noise and suspected earlier start of work at 06:30. Complaint also requested for limiting the plant operating hours from 09:00-21:00.</p>	<p>Reclamation of Central Wan Chai Bypass site area instead of part of Wanchai Development Phase II;</p> <ul style="list-style-type: none"> <li>• Two derrick barges were in operation at the time of complaint for placing 400 rockfill onto the excavation trench and for levelling the formation level to receive the pre-cast caisson seawall;</li> <li>• Flood light on the control mast of derrick barge have no lighting shields for the prevention of glare of flood lights;</li> <li>• No starting work on 7 Dec 2010 at 0630hours.</li> </ul> <ol style="list-style-type: none"> <li>2) PME used in restricted hours were checked and confirmed compliant with valid CNP no. GW-RS0870-10. The noise level recorded on 6 Dec 2010 was complied with the noise criteria during restricted hour;</li> <li>3) It was found that the occasional noise nuisance might be caused by the hitting or scratching onto the rock surface during loading down the grab onto the Grade 400 rockfill;</li> <li>4) The absence of the lighting shields at flood light results in visual glare to the complainant at night-time.</li> <li>5) Contractor was advised to minimize the finishing time of placing Grade 400 rockfill at 2100hrs and switch off all unnecessary flood lights apart from the light for the safety and security purpose;</li> <li>6) No further complaint was received after implementation of proposed measures</li> </ol>	
110415	15/04/2011	The resident, Mr Law at Victoria Centre by ICC (ICC#1-281451236)	North Point	A dust generation and a concern of mosquitoes breeding complaint in which suspected the filling operation was part of North Point Reclamation.	<ol style="list-style-type: none"> <li>1) The concerned stockpile was a working stockpile under Contract HY/209/15 and was covered at night time after work.</li> <li>2) Water spraying on the haul road and potential dust generating material at least 4 times a day was conducted by contractor that complies with the requirement.</li> <li>3) It is considered invalid but preventive actions can be taken because the stockpile is relatively large and easily visible by complainant.</li> <li>4) It was recommended that increasing the frequency of water spraying shall be conducted to all potential dust generating materials and activities. Besides, Contractor should consider to cover the idle part of the stockpile</li> <li>5) The concern of mosquitoes breeding is out the scope of EM&amp;A, the follow-up action is not reported in this monthly EM&amp;A report.</li> </ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
110419	19/04/2011	Ms Chiu at Victoria Centre at Victoria Centre by ICC (ICC# 1-272874759)	North Point	The episode of night noise on 19/4/11 and 20/4/11 at 2:50 am and the noise lasted for 30 minutes per night.	<ol style="list-style-type: none"><li>1) According to the RSS's record, there was no construction works undertaken under the EP-356/2009 during the concern time period.</li><li>2) There was no abnormal real-time noise monitoring data recorded in RTN1 - FEHD Hong Kong Transport Section Whitefield Depot which is next to the Victoria Centre.</li><li>3) It is considered as invalid complaint under this Project.</li></ol>	Closed
110617	9/06/2011	Mr. Law from Victoria Centre Management Office	North Point	An odour nuisance suspected generating from the discharge point – Channel T at Watson Road in part of the site area was related to CWB under Contract no. HY/2009/11	<ol style="list-style-type: none"><li>1) The complaint was received by ET on 13 Jun 2011. During the weekly site inspection on 7 and 17 June 2011, there was no any odour impact detected in the site area.</li><li>2) According to the site record, there was muddy water discharged from the unknown source at upstream of Channel T during heavy rainstorm. No any site surface runoff to the Channel T and out of site boundary was observed in the inspection.</li><li>3) In order to prevent muddy water washing out to the water body under heavy rainstorm, a silt curtain was installed at the outfall of the channel by Contractor. ET confirmed with the Resident Site Staff that a silt curtain was installed at the outfall of the channel to prevent muddy water washing out to the water body under heavy rainstorm. Besides, regular cleaning of refuse in the channel has been conducted by Contractor.</li><li>4) A further site investigation on 28 June 2011 revealed that no odour nuisance was detected at the upstream of the Channel T and no source of odour nuisance was identified at site. As such, it was concluded that the source of odour nuisance was not related to the Project works.</li><li>5) Although no source of odour nuisance was identified at site, the muddy water and dirt from the unknown source at upstream of Channel T may cause a potential smell during low tide and low water flow. Contractor was reminded to remove the silt curtain at the channel on non-rainy day so as to avoid the accumulation of the sediment and dirt in the water channel.</li></ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
110709	09/07/2011	Mr. Au from City Garden Management Office	North Point	A complaint letter to Contractor HY/2009/11 was raised by Cayley Property Management Limit on 9 July 2011 regarding a series of pump breakdown events at seawater intake of City Garden on 4, 6, 7 and 8 July 2011. A lot of rubbish such as plastic bags, nylon bags, nylon-wire mesh was observed sucking from the seawater intake at the seawater front of Block 7 of City Garden affecting the operation of seawater pump plant.	<ol style="list-style-type: none"><li>1) Contractor conducted formation works for installation of caisson seawall at C27, C28, C29 and C30 on 4, 6, 7 and 8 July 2011 and no dredging work was conducted during this time period</li><li>2) Water mitigation measures of an 80m long silt curtain at the site boundary in front of City Garden Relocation of silt curtain and silt curtain at the outfall of the channel were provided and maintained to accommodate the site works. All vessels are equipped with rubbish collection facilities and disposed the rubbish regularly. Also, daily cleaning actions had been taken by contractor to minimize floating refuse within the site boundary.</li><li>3) Moreover, it has been reported several times that discharged from outfall pipeline outside the site boundary near the intake of the pump maybe considered as another source of rubbish generation.</li><li>4) Referring to the record provided by Cayley Property Management Limit, the trapped rubbish was unlikely generated from the construction works. It was considered that complaint is invalid and not related to project.</li></ol>	Closed
110710	09/07/2011	Complainant by ICC (ICC no. 1-301520309)	North Point	It was received at 00:56 on 10 July 2011. There was complained a derrick barge unloading rockfill material off the shore facing the Harbour Grant HK Hotel causing noise nuisance.	<ol style="list-style-type: none"><li>1) ET confirmed with the Resident Site Staff that the complaint was referred to Contract HY/2009/15 for the loading and unloading of fill material at two barges operation in the sea at around 300m adjacent to Island Eastern Corridor (Oil Street Chainage) where is outside the Site of HY/2009/15 in the period of around 19:45 on 9 July to 1:00 on 10 July 2011.</li><li>2) The material loading and unloading operation processed in restricted hours was checked without a valid CNP. It was found that the operation was due to an unexpected water leakage of the hopper barge and considered an incident.</li><li>3) According to the incident report provided from RSS on 20 July 2011, around 7:30 pm the barge S22 was inclined slightly and slightly water leakage might occur. Due to marine safety concern, the hopper barge would open the hopper to release the contained materials in order to reduce the weight and stabilize the barge. In consider of slight water leakage, the operator decided to use the nearby Derrick Barge ST32 to help for unload the general fill materials first and the unloading operation was started at around 7:45pm, and end at around 1:00 am. Contractor was reminder to provide frequent check of vessel condition</li></ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					so as to prevent recurrent by barge defect	
110723a	23/07/2011	Ms. Law at Victoria Centre by ICC no. 1-303887687	North Point	She concerned that Highways Department published a notice in their Management Office about construction works will be conducted from 0700 hours to 2300 hours during July to December 2011 including Saturday, Sunday and public holiday.	<ol style="list-style-type: none"> <li>1) It was referred by AECOM to ET on 28 July 2011</li> <li>2) RSS confirmed that the notice was prepared by Victoria Centre's Management office to their resident and the advice was only given on the extension construction works (for Contract HY/2009/15) to 7am-9pm from Monday to Saturday except Public Holidays and Sundays.</li> <li>3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid-August 2011.</li> <li>4) No noise exceedance was recorded at construction noise monitoring station at Victoria Centre on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring.</li> <li>5) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.</li> </ol>	Closed
110723b	23/07/2011	Ms. Yau at Block 2, Victoria Centre by ICC no. 1-304013959	North Point	Reclamation work was conducted at Causeway Bay Typhoon Shelter at 7am on 23 July 2011. She complained that the works shall be started later to minimize the noise nuisance to the vicinity of the residents in early morning	<ol style="list-style-type: none"> <li>1) It was referred by AECOM to ET on 8 August 2011</li> <li>2) With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 19 and 25 July 2011 during daytime while breaking and excavation works were undertaken during monitoring</li> <li>3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am and is expected to be completed by mid-August 2011.</li> <li>4) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. The complainant was satisfied with the arrangement and no further complaint was received after proposed measures.</li> </ol>	Closed
110727a	27/07/2011	Mr. Law from Victoria Centre Management Office by ICC no. 1-304616162	North Point	It was complained by Mr. Law from Victoria Centre Management Office on 27 July 2011 regarding construction noise generated by the construction operations of	<ol style="list-style-type: none"> <li>1) It was referred by AECOM to ET on 28 July 2011</li> <li>2) RSS confirmed to start the rock breaking activities for Contract HY/2009/15 at 8am as a mitigation measure to minimize the noise nuisance in the vicinity of the residents.</li> <li>3) No noise exceedance was recorded at construction noise</li> </ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
				Central-Wanchai Bypass at noon rather than in morning at 7am.	<p>monitoring station at Victoria Centre on 25 July and 4 August 2011 during daytime while breaking and excavation works were undertaken during monitoring.</p> <p>4) In conclusion, it was related to the construction works under Contract HY/2009/15 and mitigation measure was provided. No further complaint from complainant was received after proposed the mitigation measure.</p>	
110727b	27/07/2011	Ms. Chiu by ICC no.1-304615409	North Point	Noise nuisance from the excavation works for the Highways Department adjacent to the Victoria Centre was conducted from 7am	<p>1) It was referred by AECOM to ET on 28 July 2011</p> <p>2) With reference to the construction noise monitoring at Vitoria Centre, no exceedance was recorded on 25 July and 4 and 10 August 2011 during daytime while breaking and excavation works were undertaken during monitoring.</p> <p>3) As a mitigation measure to minimize the noise nuisance in the vicinity of the residents, rock breaking activities will be started at 8am.</p>	Closed
	08/08/2011				<p>4) However, complainant did not satisfy with the response on the noise nuisance from the rock-breaking during morning in front of Victoria Centre and then further complaint via 1823 on 7 August 2011.</p> <p>5) Highways contacted the complainant on 15 August 2011 that the noisy rock breaking operation had been completed.</p> <p><i>Remarks: There will be counted as two complaints in this complaint log.</i></p>	
110810	10/08/2011	Mr. Yip by ICC no. 1 - 306740207	North Point	Muddy water was discharged from work site to the seafront near Oil Street during heavy rain. The environmental protection measures were not good enough and are needed to rectify.	<p>1) It was referred by AECOM to ET on 17 August 2011.</p> <p>2) Confirmed with RE, Muddy water was caused by a heap of earth being washed to the sea by heavy rain. The heap of earth was referred as a small stockpile placed close to the seafront in front of Oil Street within the site area under handover transition period from contract HY/2009/11 to contract HY/2009/19. The necessary mitigation measures to protect the small stockpile against rainfall were missing at the time of complaint.</p> <p>3) Due to the missing of mitigation measures to protect the small stockpile during handover transition period, loose material was washed into the harbour when heavy rain came. Muddy water was formed and dispersed in the sea that caused the water quality and visual concern to the public. The complaint was considered as valid.</p> <p>4) Contractors were advised to relocate the loose materials</p>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					away from the coastline as far as practicable. Any loose material placed which needed to be placed near the coastline shall be properly compacted or covered as appropriate. To avoid any further environmental deficiency, Contractors shall ensure all necessary environmental mitigation measures will not be missing during site area handover.	
110826	26/08/2011	Grand Hyatt and a complainant by ICC	Wan Chai	Construction noise and vibration nuisance generated from the works at Convention Avenue and inside the HKCEC1 reclamation area.	<ol style="list-style-type: none"> <li>1) Confirmed with the Resident Site Staff that the construction works were referred to the Contractor HK/2009/01.</li> <li>2) The Excavator mounted breaker at Convention Avenue and Drilling rig at HKCEC1 reclamation area were the dominant construction noise source during this period.</li> <li>3) The drilling rig at HKCEC1 reclamation area and excavator mounted breaker at Convention Avenue were then temporary suspended after received the complaint.</li> <li>4) Investigation revealed that the erected noise barrier (4m cantilevered movable noise barrier for the drilling rig and 1m movable noise barrier for the excavator mounted breaker) were not located close to the plants to provide adequate noise screening.</li> <li>5) Contractor was advised to avoid concurrent operation of construction plants at site. Further enhancement of movable noise barriers at HKCEC1 and providing noise enclosure for the excavator mounted breaker at Convention Avenue are needed.</li> <li>6) Further site investigation and checking on 31 August and 7 September 2011 revealed that the implemented noise mitigation measures were in proper and minimize the noise impact.</li> </ol>	Closed
110826A	26/08/2011	A complaint letter from Mr. Au of Cayley Property of City Garden	North Point	Harbor front adjacent to their cooling water intake suction which caused 3 times of system breakdown of the sea water pump on 9, 22 and 25 August 2011.	<ol style="list-style-type: none"> <li>1) It was referred by AECOM to ET on 29 August 2011. Confirmed with the Resident Site Staff that the           <ul style="list-style-type: none"> <li>• construction works were referred to the Contractors HY/2009/11 and HY/2009/19.</li> <li>• The pump is located on the site area of HY/2009/19</li> <li>• A temporary garbage defender was installed on 23 July 2011 by HY/2009/11 and the shape of the defender was adjusted on 8 August 2011 in order to exclude the outfall.</li> <li>• An ad hoc inspection of the effectiveness of garbage defender was conducted with RSS (CWB project</li> </ul> </li> </ol>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>team), contractor of HY/200911 and HY/2009/19 and ICon 29 August 2011. Inspection report of it was submitted to RSS on 19 September 2011.</p> <ul style="list-style-type: none"> <li>• Daily cleaning near the water intake was conducted twice a day by contractor HY/2009/19.</li> <li>• In response to City Garden request, the contractors have set up the temporary garbage defender in function and collect the floating refuses, but cannot eliminate all refuses, in particular the refuse coming from the seabed</li> </ul> <p>2) According to the complaint letter from Cayley Property, the outcomes of the preventive measures were not complying with their expectation.</p> <p>3) During on-site inspection, floating refuses observed occasionally outside the garbage defender. No conclusion could be made for the source of these floating refuses. On the other hand, some of the refuses were observed floating behind the garbage defender during investigation.</p> <p>4) All daily cleaning actions had been taken by contractor to minimize floating refuse inside the construction site.</p> <p>5) It was noted that the cooling water intake was accessible to the public. As such, fish breeding and fishing activities were observed even though a notice has already hoisted. Also, tripping of rubbish by the passers-by could result in a lot of rubbish accumulated around the intake point.</p> <p>6) Referring to the record provided by CPML, there were a lot of nylon/ plastic bags and nylon wire mesh that matched those rubbishes generated from the public activities.</p> <p>7) Contractors have fulfilled the requirement of site cleanliness and no exceedance was recorded during Water Quality Monitoring. It is considered the cause of this complaint is not related to project and environmental issue in this project as well. No more complaint received after ad-hoc inspection</p>	
111014	14/10/2011	The complainant, Ms. Tam complained via hotline 1823	Wan Chai	The polluted fumes and exhaust from the excavation by sub-contractor of CEDD on pedestrian way outside no.25 Harbour Road (in front of the Harbour Centre)	<p>1) RSS notified ET to carry out investigation on 17 October 2011.</p> <p>2) ET confirmed with the Resident Site Staff that the location of the excavator was within site area of Contract no. HK/2009/02 undertaking the water cooling main re-provision works along the Harbour Road. The plants including the excavator have been checked before using</p>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>at the site. However, the polluted fumes and exhausted from the excavator was caused due to insufficient maintenance of the plant after using at site.</p> <p>3) After receiving the complaint, the excavator was then removal off-site for checking and maintenance works on 17 October 2011.</p> <p>4) Contractor was reminded to enhance regular checking and maintenance to all plants at site.</p> <p>5) RSS has replied to the complainant on the arrangement of the measures taken on 17 October 2011. Complainant was satisfied with the response and follow-up action taken by the Contractor.</p>	
111104	04/11/2011	Mr. Liu from LCS D complained via Contractor Complaint Hotline	Wan Chai	Complain about a tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road, the status is not healthy and roof ball of two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue were half cut.	<p>1) ET confirmed with the Resident Site Staff that</p> <ul style="list-style-type: none"> <li>A tree near the site of pipe installation works outside Wan Chai Swimming Pool at Harbour Road is the Tree no. TA1122 under Contract no. HK/2009/02. Leaves of a branch of this tree were shrivelled.</li> <li>Two trees inside the site near Renaissance Hong Kong Harbour View Hotel at Convention Avenue are the tree nos. A160 and A161 under Contract no. HK/2009/01. Part of roof ball of these two trees was covered by the metal plate.</li> </ul> <p>2) Independent Tree Specialists for these two inspected the trees. Contractor HK/2009/01 has taken the measure as recommend downgrading the soil level around the trunk base. Reinstating of the ground works will be conducted in mid-December 2011. For the tree no. TA1122 under Contract no. HK/2009/02, the brown leaves were removed and fenced the tree with orange net is provided to prevent damage of tree trunk by construction works. The distance between the tree and the edge of the trench is kept approximate 2m. Two Contractors were reminded to carry out regular watering to the trees within their site area.</p>	Waiting RSS respond
111106	06/11/2011	Police officer	Wan Chai	Construction noise generated from the site at about 6:30 a.m on 6 November 2011 and require to stop the machine operation	<p>1) According to the information reported by Contractor, one BC cutter and hoist were operated for Diaphragm Wall construction of Shatin-Central Link to inspect bentonite pipes and ensure no damages and all the joints are tightened in good position. Then, the subcontractor for Diaphragm wall, SAMBO Korean foreman stopped the engine of the BC cutter immediately. The police officer recorded the details and HKID number of the foreman and then left. Due to the different language communication between the police officer and the Korean foreman, no</p>	Keep in view for three months from the date of complaint received



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>CNP was checked by the police officer.</p> <p>2) ET confirmed with the Resident Site Staff that same issue was also raised out by RSS at about 7:00a.m on the same day. Besides, it was confirmed that there is no valid Construction Noise Permit for the conducted construction works in the period between 2300 and 0700.</p> <p>3) Due to insufficient communication between Contractor HK/2009/01 and their Korean Sub-contractor, Korean Sub-contractor had not notified to Contractor before carrying out the inspection of the BC cutter, hoists and bentonite pipes at about 6:00a.m to ensure no damages and all the pipe joints should be tightened and in good position.</p> <p>4) Contractor was advised to enhance the communication between Contractor and sub-contractor and provide sufficient environmental training to all foreman and operators on restricted hour operation. Furthermore, Construction Noise Permit should be checked and in place for the construction works during restricted hour</p> <p>5) This complaint was considered in relation to the conducted construction works during restricted hours without valid Construction Noise Permit. No more construction works were conducted during night time period. The construction works will be conducted in accordance with the time period stated in valid CNP. This complaint will be kept in view of any follow-up action from the relevant government activities.</p>	
120405	05/04/2012	N/A	North Point	A complaint regarding excessive noise from construction sites of CBTS was observed daily before 7:30am except on public holidays, and the noise source was mainly from piling works. The complainant requested that construction works should start after 8:30am to avoid nuisance to nearby residents and a speedy follow-up and reply.	<p>1) RSS notified ET on 5 April 2012.</p> <p>2) ET confirmed with the Resident Site Staff that no piling works were performed during the concerned period.</p> <p>3) After reviewing the results of noise monitoring (M2b and M3a), no exceedance was recorded during daytime period and the noise level was below 75dB(A). Site inspection for HY/2009/15 was conducted on 10 April 2012. The condition of noise mitigation measures around CBTS was found satisfactory. RSS confirmed that no pilings were performed during the concerned period. The major works included drilling, diaphragm wall construction and excavations.</p> <p>4) HyD made a reply to the complainant on 16 April 2012 via 1823. HyD replied that the current works at CBTS were drilling, diaphragm wall construction and deep excavations. In order to minimize the noise generated</p>	Closed



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					from the above works, the Contractor had erected temporary noise barriers and provided noise blankets on plants. RSS would continue to work with the Contractor on the effectiveness of the environmental mitigation measures implemented on site. No further complaint was received after the response.	
130308	06/03/2013	ICC Case#1-407181502	Tin Hau	A complaint regarding the dropping of fine rock material into surrounding waterbody was observed during rock breaking operation with two excavators in active operation at the Eastern Breakwater of Causeway Bay Typhoon Shelter near the North Point lighthouse.	<p>1) RSS notified ET on 8 March 2013</p> <p>2) ET confirmed with RSS that excavation works, installation of buoy, flashing light and silt curtain and dredging works were undertaken at Eastern Breakwater during the concerned period on 6 March 2013. One backhoe equipped with breaker and one derrick barge were confirmed in operation while another backhoe was at idle during the concerned period on 6 March 2013.</p> <p>3) Reviewing the photo record provided by RSS, the condition of the silt curtain deployed around the Eastern Breakwater on 6 March 2013 was found to be in good condition. It is considered that the silt curtain was properly in place during the concerned period and the concerned act of dropping of fine rock material was confined within the silt curtain boundary without adverse impact to the nearby water quality.</p> <p>Further follow up was conducted on 12 March 2013 during weekly environmental audit inspection, the silt curtain deployed around the concerned area was found to be maintained in good condition and the water quality at the concerned work area was generally satisfactory. No violation of the Environmental Permit condition was found.</p> <p>The contractor was advised and committed to implement preventive measures to minimize the potential impact of work including conducting regular diver check to ensure the integrity and the extend of silt curtain deployment and to provide adequate back up stock of silt curtain for emergency use.</p>	Closed
140612	12/06/2014	EPD ref: EP/860/F2/24 Annex IV	Wan Chai	The complaint is regarding to the water quality of the waterfront outside the Hong Kong Academy for Performing Arts Theatre Block, where a large piece of muddy water was found.	<p>1) WSII RSS team notified ET on 12 June 2014; Notification letter from EPD (ref: EP/860/F2/24 Annex IV) was received by ET on 13 June 2014.</p> <p>2) ET confirmed with RSS that neither marine construction works nor barge operation was conducted at the concerned location during the time of complaint. With respect to the complaint case, muddy dispersion was observed at HKCEC2W works area on 12 June 2014, and</p>	Interim Report was submitted to EPD on 20 June 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>the dispersion was observed partly extended beyond the outermost layer silt curtain at 1000hrs. Immediate follow up action was requested.</p> <p>3) It is considered that Contractor's mitigation measures would require further review on the effectiveness to avoid seepage of muddy dispersion such as regular diver inspection check and daily visual checking of silt curtains.</p> <p>Additional silt curtain at marine access zone was installed by Contractor on 12 June 2014 and the double layer silt curtain were generally in order. Follow-up inspection was further conducted on 16 June 2014.</p> <p>The Contractor's investigation report on the complaint case was submitted to EPA via email on 18 June 2014.</p>	
140723	21/07/2014	ICC Case Ref: 2-341537112	Works area opposite to Ngan Tao Building	The complaint is regarding to construction noise impact to the complainant who could not sleep due to work and machine at the project site opposite to the Ngan Tao Building.	<p>1) Construction noise impact referred by RSS was received by ET on 25 July 2014</p> <p>2) ET confirmed with RSS that horizontal cutting and removal of D-wall at Eastern, Southern and Northern side of TS2 was undertaken by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter before 23:00hrs on 20 July 2014 that total 3 numbers of derrick lighter and 3 numbers of saw cut machine were in operation, and removal of D-wall at Panel S30A-1 of TS2 was undertaken by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter around 00:25hrs to 00:56hrs on 21 July 2014 that total 1 number of derrick lighter was in operation.</p> <p>3) According to the relevant site records under Contract HY/2009/15, before 23:00hrs on 20 July 2014, horizontal cutting and removal of Diaphragm Wall at Eastern, Southern and Northern side of TS2 was conducted under HY/2009/15 within Causeway Bay Typhoon Shelter. Total 3 nos. of derrick lighter and 3 nos. of saw cut machine were in operation at the above period. From around 00:25hrs to 00:56hrs on 21 July 2014, removal of D-wall at Panel S30A-1 of TS2 was undertaken by Contractor of HY/2009/15 within Causeway Bay Typhoon Shelter. Total 1 no. of derrick lighter was found operating at the above period</p> <p>4) It was considered the condition of CNP GW-RS0592-14 was not fulfilled by the Contractor of HY/2009/15. "From 00:25hrs to 00:57hrs on 21 July 2014, the PME(s) (1 no. of Derrick Lighter) on-site could not follow with any given PME grouping requirement(s) as stated in condition 3.a. and condition 3.d. in no. GW-RS0592-14."</p>	<p>Final report (Issue1) issued on 31 July 2014.</p> <p>Further to complainant follow-up, Final report (Issue2) Issued on 12 Aug 2014.</p>



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>Notwithstanding the above, according to the site recorded provided by the RSS, the derrick lighter was found malfunction at around 23:00hrs on 20 July 2014 while the diaphragm wall cutting procedure was incomplete. Under safety and navigation consideration, the completion of diaphragm wall removal was necessary and of imminent need.</p> <p>5) The Contractor of HY/2009/15 was advised to review the construction sequence and emergency response procedure for construction activities during restricted hours and night time period to allow for sufficient buffer time for work completion such that the Construction Noise Permit would be followed. Furthermore, the Contractor of HY/2009/15 was suggested to conduct throughout checking of PME used on site prior to work commencement to minimize the potential malfunctioning of PME during the course of work which affect the duration of works.</p>	
141016	14/10/2014	<p>EPD Ref.: EP860/E2/24 Annex IV</p> <p>ICC complaint received by ET on 10 October 2014</p>	Work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	Construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.	<p>A public complaint regarding construction noise impact referred by EPD was received by ET on 16 October 2014 (EPD Ref.: EP860/E2/24 Annex IV dated 16 October 2014).</p> <p>The complainant reported that construction noise like piling works was heard on 14 October 2014 night until 23:45 hrs. It was suspected that the noise was emanated from the work site next to new Wan Chai Ferry Pier and opposite to Wan Chai Sports Ground.</p> <p>ET confirmed with the Resident Site Staff that From 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.</p> <p>Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</p> <p>From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.</p> <p>Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</p>	<p>Interim investigation report submitted to EPD on 23 October 2014.</p> <p>Updated interim investigation with supplementary information submitted to EPD on 17 November 2014</p>



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway.</p> <p>Total one scissor platform and two hand held drills (battery) were in operation.</p> <p>From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road.Total one crane lorry was in operation.</p> <p>According to the relevant site records under Contract HK/2009/02, from 19:00hrs to 23:00hrs on 14 October 2014, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area. Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</p> <p>From 23:00 hrs to 05:00 hrs, dredging works was conducted under Contractor of HK/2009/02 at WCR3 Area.Total one grab dredger was in operation. Mitigation measures including provision of steel sheeting screening to the power generation part of the grab dredger was implemented by the Contractor of HK/2009/02.</p> <p>From 23:00 hrs to 06:00hrs, panel replacement works was conducted under Contractor of HK/2009/02 at the Temporary Covered Walkway. Total one scissor platform and two hand held drills (battery) were in operation.</p> <p>From 23:00 hrs to 06:00hrs, trial pit works was conducted under Contractor of HK/2009/02 at Hung Hing Road. Total one crane lorry was in operation.</p> <p>In view of the above findings, no direct information associated with the noise concern was considered available.</p>	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
141110	07/11/2014	EPD Ref.: H05/RS/000278 15-14  EPD complaint received by ET on 10 November 2014	Construction site at old Wan Chai Ferry Pier	Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool.	<p>A public complaint regarding odour concern referred by EPD was received by ET on 07 November 2014 (EPD Ref.: H05/RS/00027815-14 dated 10 November 2014).</p> <p>The complainant reported that Malodour of construction plant exhaust from the construction site at old Wan Chai Ferry Pier was scented that affecting the swimmers at Wan Chai Swimming Pool.</p> <p>ET confirmed with the Resident Site Staff that</p> <p>ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool).</p> <p>Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated.</p> <p>Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier.</p> <p>Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.</p> <p>Dredging works was conducted on 7 November 2014 during daytime at WCR3 (East of old Wan Chai Ferry Pier)</p> <p>Total 1 no .of dredger, 1 no. of hopper and 1 no. of tug boat were operated.</p> <p>According to the relevant site records under Contract HK/2009/02, ELS works was conducted on 7 November 2014 during daytime at Portion 2 (Area oppsite to WanChai Swimming Pool). Total 3 nos. of excavators, 2 nos. of crawler cranes, 2 nos. of generator, 1 no. of crane lorry and 2 no. of dump trucks were operated. Demolition works was conducted on 7 November 2014 during daytime at West of old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. of tug boat were operated.</p> <p>Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site. The condition of chemical waste storage was considered satisfactory and no malodour was identified. Despite no information related to malodour was identified, the Contractor was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.</p>	<p>Interim investigation report submitted to EPD on 17 November 2014.</p> <p>EPD advised no comment on the interim report and case closed on 1 Dec 2014.</p>



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Based on the relevant information provided by RSS, despite no information associated with the malodour concern was identified after investigation, the Contractor was reminded to conduct regular checking on the condition of PME used on site to ensure only well maintained PME are used on site The interim report would be submitted to EPD on 17 November 2014.	
141113	12/11/2014	EPD Ref.: H05/RS/000282 53-14  EPD complaint received by ET on 13 November 2014	Construction site at old Wan Chai Ferry Pier	Malodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians.	<p>A public complaint regarding odour concern referred by EPD was received by ET on 13 November 2014 (EPD Ref.: H05/RS/00028253-14 dated 13 November 2014). The complainant reported that Malodour and dark smoke emission from an excavator located at the construction site at old Wan Chai Ferry Pier was observed that affecting the pedestrians. (Contract HK/2009/02)</p> <p>ET confirmed with the Resident Site Staff that demolition works was conducted under Contract HK/2009/02 on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated.</p> <p>According to the relevant site records under Contract HK/2009/02, demolition works was conducted on 12 November 2014 during daytime at old Wan Chai Ferry Pier. Total 2 nos. of excavators, 1 no. of derrick barge and 1 no. tug boat were operated.</p> <p>In addition, investigation found that due to malfunctioning of one of the excavators deployed at old Wan Chai Ferry Pier, dark smoke was emitted from the defective excavator for a short period of approximately 30 seconds at around 15:00 hrs on 12 November 2014. The operation of excavator was immediately suspended and followed by repair works. The normal operation of the excavator was resumed after repair.</p> <p>Follow-up inspection was conducted during weekly environmental inspection on 13 November 2014, no dark smoke emission was observed from the PMEs operating on-site and the Contractor of HK/2009/02 was reminded to conduct regular checking on the condition of PMEs to ensure only well maintained PMEs are used on site.</p>	Interim investigation report submitted to EPD on 19 November 2014.  EPD advised no comment on the interim report and case closed on 8 Dec 2014.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
141121	Not Specified	<p>EPD Ref: H08/RS/28263-14</p> <p>EPD complaint information and findings was received by ET via email on 21 Nov 2014</p>	Causeway Bay Typhoon Shelter	Resident in Hing Fat Street complaining about loud noise from dredging work in CBTS up to 10pm at night.	<p>EPD received a construction noise complaint from dredging works at Causeway Bay Typhoon Shelter and a resident in Hing Fat Street complaining about loud noise from dredging work in CBTS up to 10pm at night.</p> <p>EPD investigation found that the operation of a derrick barge is covered by CNP no. GW-RS0701-14.</p> <p>EPD reminded the Contractor of HY/2011/08 to ensure the work strictly follow the permit conditions and endeavor to minimize the noise as so not to disturb the nearby residents.</p>	Complaint case handled by EPD and relevant investigation findings was sent to ET on 21 November 2014
150127	21 Jan 2015	<p>EPD complaint (EPD Ref.: H05/RS/00001725-15) received by ET on 27 January 2015 and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015</p>	A portion of Hung Hing Road immediately to the east of Marsh Road near SPCA	Construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public.	<p>A public complaint regarding air quality impact referred by EPD was received by ET on 27 January 2015 (EPD Case Ref.: H05/RS/00001725-15 dated 27 January 2015) and further information from EPD regarding the updated location under complaint was received by ET on 30 January 2015. The complainant reported that construction dust and grit was emitted from the construction site to the carriageway causing nuisance to the public.</p> <p>ET confirmed with the Resident Site Staff that the major construction activities around the concerned location conducted on 21 January 2015 include breaking of seawall blocks and D-wall at TPCWAW; concreting, grouting and drilling works at TPCWAW;reclamation/ backfilling works at TPCWAW</p> <p>Mitigation measures implemented by the Contractor for the above construction works include spraying haul road with water; covering bagged cement with tarpaulin; providing three sided and top covering for grouting stations; providing water spraying to dusty activities such as breaking works</p> <p>According to the relevant site records, breaking of seawall blocks and D-wall, concreting, grouting and drilling works and reclamation/ backfilling works were</p>	Interim report submitted to EPD on 9 February 2015



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					<p>conducted at TPCWAW. Dust mitigation measures including spraying haul road with water, covering bagged cement with tarpaulin, providing three sided and top covering for grouting stations and water spraying to dusty activities such as breaking works were implemented by the Contractor of HY/2009/15 near the concerned location on 21 January 2015.</p> <p>Follow-up investigation was conducted on 27 January 2015 during weekly environmental inspection, dust mitigation measures including water spraying for dusty haul road and major dust generation works; and provision of three sides and top covering for grouting station were confirmed in place.</p> <p>In addition, based on the review of the monitoring data of the monitoring station located at the concerned location raised by the complainant, namely monitoring station CMA3a , no action or limit level exceedance was recorded during air quality monitoring conducted on 20 and 21 January 2015. Nevertheless, the Air Quality Health Index (AQHI) recorded by EPD across Western District and Eastern District on the complaint date was ranged from 4 to 10+ indicating a severely high concentration of ambient air pollutants.</p> <p>As such, the site condition under Contract HY/2009/15 at the concerned location was considered to be generally satisfactory and no non-conformity related to cumulative air quality impact was observed. Nevertheless, in view of the public concern, the contractor was reminded to enhance the dust mitigation measures implemented to minimize potential nuisance to nearby public.</p>	
150622	18 June 2015	EPD Ref.:H05/RS/ 00015054-15 dated 8 June	A mooring location near shore and at location outside Wan Chai Sports	Dark smoke and malodour emission was observed from a hopper barge moored near shore and	A public complaint regarding dark smoke and malodour concern referred by EPD was received by ET on 22 June 2015 (EPD Ref.: H05/RS/00015054-15 dated 22 June 2015). The complainant reported that dark smoke and malodour emission was observed from a hopper barge	Interim report submitted to EPD on 29 June 2015



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
		2015	Ground	other construction plants under operation from the reclamation construction site	<p>moored near shore and other construction plants under operation from the reclamation construction site with Contract no. HK/2009/02 at location outside Wan Chai Sports Ground caused air pollution. The complainant alleged that the said situation had been observed for a prolonged period.</p> <p>ET confirmed with the Resident Site Staff that reinforced bar fixing and concreting work (on 17 June 2015 only) were conducted at Portion 2 from 15 June 2015 to 19 June 2015. Total 3 nos. of mobile crane were in operation. On 17 June 2015, one no. of concrete pump truck and two nos. of concrete mixer were in operation. Excavation and Lateral Support was conducted at Portions 3 &amp; 4 from 15 June 2015 to 19 June 2015. Total 4 nos. of excavator, 2 nos. of truck and 2 nos. of crawler crane were in operation. In addition, on 15 June 2015, 17 June 2015 and 19 June 2015, 1 no. of derrick barge was moored near Portions 3 &amp; 4 for transportation of the excavated material away from site.</p> <p>According to the relevant site records under Contract HK/2009/02, from 15 June 2015 to 19 June 2015, reinforced bar fixing and concreting work (on 17 June 2015 only) were conducted at Portion 2 and total 3 nos. of mobile crane, one no. of concrete pump truck (on 17 June 2015 only) and two nos. of concrete mixer (on 17 June 2015 only) were in operation; excavation and lateral support was conducted at Portions 3 &amp; 4 and total 4 nos. of excavator, 2 nos. of truck and 2 nos. of crawler crane were in operation. Based on relevant site record, no hopper barge was moored under Contract HK/2009/02 around the concerned location while 1 no. of derrick barge was moored under Contract HK/2009/02 near Portions 3 &amp; 4 for transportation of the excavated material from Portions 3 &amp; 4 away from site on 15 June 2015, 17 June 2015 and 19 June 2015 respectively.</p> <p>Follow-up inspection was conducted during weekly</p>	



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					environmental inspection on 25 June 2015, no dark smoke and malodour emission was observed from the PMEs operating on-site. A derrick barge was observed moored near Portions 3 & 4 and excavated material was transferred to the derrick barge by the excavators on land without barge operation and no particular dark smoke and malodour emission was observed. Nevertheless, the Contractor was reminded to conduct regular checking on the condition of the derrick barge and other PMEs deployed on site to ensure only well maintained PMEs are used to avoid potential dark smoke and maldour emission affecting nearby public.	
150723	20 July 2015	EPD Ref.:H05/RS/00018040-15 dated 23 July 2015	Ex-Wanchai Ferry Pier near 720 & 722 Bus stop	Malodour from marine sediment	<p>A public complaint regarding malodour referred by EPD was received by ET on 23 July 2015 (EPD Ref.: H05/RS/00018040-15 dated 23 July 2015).</p> <p>The complainant reported that malodour from marine sediment was scented at ex-Wanchai ferry pier near route 720 &amp; 722 bus stop. (Contract HK/2009/02).</p> <p>ET confirmed with the Resident Site Staff that Rockfill placing works was conducted by one derrick barge at the concerned location (WCR3) under Contract HK/2009/02 on 20 July 2015. No marine sediment was stored or placed on site at the concerned location under Contract HK/2009/02 on 20 July 2015.</p> <p>According to the relevant site records under Contract HK/2009/02, rockfill placing works was conducted by one derrick barge at WCR3 area on 20 July 2015 and no marine sediment was stored or placed on site at the concerned location on the concerned date.</p> <p>Follow-up inspection was conducted during weekly environmental inspection on 29 July 2015. No marine sediment was observed stored or placed at the concerned location while it was noted that a culvert outfall with potential odour concern is located adjacent to the concerned location.</p>	Interim report submitted to EPD on 30 July 2015.



Complaint Log No.	Date of Complaint	Received From and Received By	Location of Complainant	Nature of Complaint	Outcome	Status
					Nevertheless, the Contractor was reminded to review the handling procedures in case of any future marine sediment handling at the concerned location and to consider the implementation of mitigation measures as appropriate to minimize potential malodour impact to nearby public.	



***Appendix 10.1***

***Construction Programme of Individual Contracts***

















Activity ID	Activity Name	Remaining Duration	Start	Finish	2015											
					August				September				October			
					09	16	23	30	06	13	20	27				
<b>3MRP - Aug 2015 to Nov 2015</b>																
<b>02 - PRE-CONSTRUCTION WORKS</b>																
<b>02.3 - Method Statement / Shop Drawings</b>																
0230-1380	MS Landscape Deck Structure - Submission	28	20-Aug-15	16-Sep-15	MS Landscape Deck Structure - Submission											
0230-1390	MS Landscape Deck Structure - ER Review & Comment	28	17-Sep-15	14-Oct-15	MS Landscape Deck Structure - ER Review & Comment											
0230-1400	MS Landscape Deck Structure - Resubmission	28	15-Oct-15	11-Nov-15	MS Landscape Deck Structure - Resubmission											
0230-1611	MS Noise Semi Enclosure - Submission	54	20-Jul-15 A	12-Oct-15	MS Noise Semi Enclosure - Submission											
0230-1612	MS Noise Semi Enclosure - ER Review / Comment	28	13-Oct-15	09-Nov-15	MS Noise Semi Enclosure - ER Review / Comment											
0230-1690	MS Approach Ramp - ER Approval	14	01-Feb-15 A	02-Sep-15	MS Approach Ramp - ER Approval											
0230-2280	MS EVB Basement & Mezzanine Construction - No Adverse Comment	0	20-Jul-15 A	02-Aug-15 A	MS EVB Basement & Mezzanine Construction - No Adverse Comment											
0230-2330	MS for Connection of EVB and EVA - Submission	10	10-Mar-15 A	29-Aug-15	MS for Connection of EVB and EVA - Submission											
0230-2340	MS for Connection of EVB and EVA - ER Review & Comment	12	30-Aug-15	10-Sep-15	MS for Connection of EVB and EVA - ER Review & Comment											
0230-2350	MS for Connection of EVB and EVA - Resubmission	6	11-Sep-15	16-Sep-15	MS for Connection of EVB and EVA - Resubmission											
0230-2360	MS for Connection of EVB and EVA - ER No Adverse Comment	10	17-Sep-15	26-Sep-15*	MS for Connection of EVB and EVA - ER No Adverse Comment											
0230-2370	MS for Contruction of New IEC Westbound Bridge - Submission	0	20-Jul-15 A	29-Jul-15 A	MS for Contruction of New IEC Westbound Bridge - Submission											
0230-2380	MS for Contruction of New IEC Westbound Bridge - ER Review & Comment	0	30-Jul-15 A	10-Aug-15 A	MS for Contruction of New IEC Westbound Bridge - ER Review & Comment											
0230-2390	MS for Contruction of New IEC Westbound Bridge - Resubmission	0	11-Aug-15 A	19-Aug-15 A	MS for Contruction of New IEC Westbound Bridge - Resubmission											
0230-2400	MS for Contruction of New IEC Westbound Bridge - ER No Adverse Comment	0	20-Jul-15 A	29-Jul-15 A	MS for Contruction of New IEC Westbound Bridge - ER No Adverse Comment											
<b>02.4 - Contractor's Design and Build Items</b>																
0240-1180	HGHK Permanent Carpark Design - ER/HGHK Review and Comment	50	20-Aug-15	08-Oct-15	HGHK Permanent Carpark Design - ER/HGHK Review and Comment											
0240-1190	HGHK Permanent Carpark Design - Resubmission	50	09-Oct-15	27-Nov-15	HGHK Permanent Carpark Design - Resubmission											
0240-1270	Landscaping Design - Submission	90	20-Aug-15*	17-Nov-15	Landscaping Design - Submission											
0240-1630	Green Roof & Wall Minimum 2 years Establishment	501	18-Apr-15 A	19-Apr-17	Green Roof & Wall Minimum 2 years Establishment											
<b>02.5 - Bridge Segment/Beam Off-site Precasting</b>																
0250-2620	Precast Beam Bridge C1 2122-E	0	23-Jun-15 A	31-Jul-15 A	Precast Beam Bridge C1 2122-E											
0250-2640	Precast Beam Bridge C1 2122-F	0	11-Jul-15 A	07-Aug-15 A	Precast Beam Bridge C1 2122-F											
0250-2660	Precast Beam Bridge E E3E2-A	0	10-May-15 A	15-Aug-15 A	Precast Beam Bridge E E3E2-A											
0250-2860	Precast Beam Bridge F5 - 14	0	01-Jun-15 A	13-Aug-15 A	Precast Beam Bridge F5 - 14											
0250-2880	Precast Beam Bridge F5 - 15	0	08-Jun-15 A	31-Jul-15 A	Precast Beam Bridge F5 - 15											
0250-2900	Precast Beam Bridge F5 - 03	0	23-Jun-15 A	27-Jul-15 A	Precast Beam Bridge F5 - 03											
0250-2920	Precast Beam Bridge F5 - 04	0	30-Jun-15 A	27-Jul-15 A	Precast Beam Bridge F5 - 04											
0250-2940	Precast Beam Bridge F5 - 05	0	10-Jul-15 A	13-Aug-15 A	Precast Beam Bridge F5 - 05											
0250-2960	Precast Beam Bridge F5 - 06	0	15-Jul-15 A	07-Aug-15 A	Precast Beam Bridge F5 - 06											
0250-2980	Precast Beam Bridge F5 - 07	0	22-Jul-15 A	14-Aug-15 A	Precast Beam Bridge F5 - 07											
0250-3000	Precast Beam Bridge F5 - 08	0	28-Jul-15 A	16-Aug-15 A	Precast Beam Bridge F5 - 08											
0250-3020	Precast Beam Bridge F5 - 09	0	04-Aug-15 A	14-Aug-15 A	Precast Beam Bridge F5 - 09											
0250-3030	Precast Beam Bridge F5 - 10	0	08-Aug-15 A	16-Aug-15 A	Precast Beam Bridge F5 - 10											
0250-3035	Completion of Beam Off-Site Pre casting	0		16-Aug-15 A	Completion of Beam Off-Site Pre casting											
0250-3580	Bridge F1C Pier 36 T-span Segment Off-site Casting (13 nos.)	17	10-Jun-15 A	08-Sep-15	Bridge F1C Pier 36 T-span Segment Off-site Casting (13 nos.)											
0250-3600	Bridge F1C Pier 37 T-span Segment Off-site Casting (11 nos.)	3	16-Jul-15 A	22-Aug-15	Bridge F1C Pier 37 T-span Segment Off-site Casting (11 nos.)											
0250-3620	Bridge F1C Abut D12 End-span Segment Off-site Casting (7 nos.)	0	21-Jul-15 A	12-Aug-15 A	Bridge F1C Abut D12 End-span Segment Off-site Casting (7 nos.)											
0250-3640	Bridge F1C Pier 38 End-span Segment Off-site Casting (6 nos.)	6	18-Jun-15 A	26-Aug-15	Bridge F1C Pier 38 End-span Segment Off-site Casting (6 nos.)											
0250-3720	Bridge F3C Pier 41 T-span Segment Off-site Casting (13 nos.)	29	10-Apr-15 A	22-Sep-15	Bridge F3C Pier 41 T-span Segment Off-site Casting (13 nos.)											
0250-3740	Bridge F3C Pier 42 T-span Segment Off-site Casting (11 nos.)	15	18-Apr-15 A	05-Sep-15	Bridge F3C Pier 42 T-span Segment Off-site Casting (11 nos.)											
0250-3760	Bridge F3C Pier 40 End-span Segment Off-site Casting (5 nos.)	16	10-Apr-15 A	07-Sep-15	Bridge F3C Pier 40 End-span Segment Off-site Casting (5 nos.)											
0250-3780	Bridge F3C Pier 43 End-span Segment Off-site Casting (6 nos.)	19	22-May-15 A	10-Sep-15	Bridge F3C Pier 43 End-span Segment Off-site Casting (6 nos.)											
0250-3860	Bridge F1B2 - Abut D12 Segment - 6 nos. (S2)	19	05-Sep-15	29-Sep-15	Bridge F1B2 - Abut D12 Segment - 6 nos. (S2)											
0250-3880	Bridge F1B2 - Pier F1B2 Segment - 13 nos. (S1)	40	11-Sep-15	30-Oct-15	Bridge F1B2 - Pier F1B2 Segment - 13 nos. (S1)											
0250-3920	Bridge F1B2 - Pier F3B2 Segment - 6 nos. (S2)	19	07-Oct-15	30-Oct-15	Bridge F1B2 - Pier F3B2 Segment - 6 nos. (S2)											
0250-3940	Bridge F2B - Pier F3B2 Segment - 5 nos. (S2)	16	06-Nov-15	25-Nov-15	Bridge F2B - Pier F3B2 Segment - 5 nos. (S2)											
<b>02.6 - Fabrication &amp; Delivery of Noise Enclosure</b>																
0260-5000	Int. Noise Enclosure Main + Sub Frames Fab / Del	105	01-Jun-15 A	23-Dec-15	Int. Noise Enclosure Main + Sub Frames Fab / Del											
0260-5010	Int. Noise Enclosure Noise Panel Fab / Del	122	19-Jan-15 A	14-Jan-16	Int. Noise Enclosure Noise Panel Fab / Del											
<b>05 - SECTION 2 &amp; 2A OF THE WORKS</b>																
<b>05.1 - Cut &amp; Cover Tunnel Ch 4855-4932 (APS Footprint)</b>																

- Remaining Level of Effort
  - Actual Level of Effort
  - Actual Work
  - Remaining Work
  - Critical Remaining Work
- ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme ( 20 Aug to 19 Nov 2015 )**

Activity ID	Activity Name	Remaining Duration	Start	Finish	2015											
					August				September				October			
					09	16	23	30	06	13	20	27				
<b>05.1.1 - D-Wall Construction</b>																
0511-1600	D-Wall Interface Coring	0	16-May-15 A	25-Jul-15 A												
0511-1620	D-Wall Grouting/Pressure Grouting	0	26-Jul-15 A	31-Jul-15 A	sure Grouting											
<b>05.1.3 - APS &amp; Tunnel Structure</b>																
0513-3060	APS Basement (Bay 21-South) - Staircase Landing 8 > Staircase Landing 12	11	07-Jul-15 A	01-Sep-15	APS Basement (Bay 21-South) - Staircase Landing 8 > Staircase Landing 12											
0513-3080	Tunnel Level - South Side Additional Beam at Bay 21	5	20-Aug-15	25-Aug-15	Tunnel Level - South Side Additional Beam at Bay 21											
0513-3100	Reinstate Temporary Opening of Base Slab > Bay 18	9	22-Aug-15	01-Sep-15	Reinstate Temporary Opening of Base Slab > Bay 18											
0513-3105	Reinstate Temporary Opening of OHVD & Roof Slab > Bay 18	6	22-Aug-15	28-Aug-15*	Reinstate Temporary Opening of OHVD & Roof Slab > Bay 18											
0513-3140	APS Basement (Bay 21-South) - Partition wall	0	07-Apr-15 A	31-Jul-15 A	21-South) - Partition wall											
<b>05.1.4 - Tunnel Structure</b>																
0514-2040	Weak Seam Rectification works for sub-standard D-Wall	0	10-Mar-15 A	31-Jul-15 A	ion works for sub-standard D-Wall											
<b>05.1.5 - EVB Sub-structure &amp; Tunnel</b>																
0515-1060	Tunnel Roadside/Profile Barrier and Cable Trough Portion VIII B & IX B	0	16-Jun-15 A	31-Jul-15 A	ile Barrier and Cable Trough Portion VIII B & IX B											
0515-1061	Roadside Barrier - Service Trough/Steel Angle/Precast Concrete Cover	0	20-Jul-15 A	31-Jul-15 A	ervice Trough/Steel Angle/Precast Concrete Cover											
0515-1120	EVB Basement - Col/Partition Wall (Reb. Fix) > Zone 1A: GL1-2/A-E, 2-3/B-E, 3-6/C	4	13-Jul-15 A	24-Aug-15	EVB Basement - Col/Partition Wall (Reb. Fix) > Zone 1A: GL1-2/A-E, 2-3/B-E, 3-6/C-F, 4-6/F-J											
0515-1140	EVB Basement - Col/Partition Wall (Fwk) > Zone 1A to Mezz (-1.40) Soffit	7	03-Aug-15 A	27-Aug-15	EVB Basement - Col/Partition Wall (Fwk) > Zone 1A to Mezz (-1.40) Soffit											
0515-1160	EVB Basement - Col/Partition Wall (Conc) > Zone 1A to Mezz (-1.40) Soffit	2	28-Aug-15	29-Aug-15	EVB Basement - Col/Partition Wall (Conc) > Zone 1A to Mezz (-1.40) Soffit											
0515-1180	EVB Basement - Mezz Slab & Beam (Lv -1.4) - (Falsework/Fwk) > Zone 1A	10	17-Aug-15 A	10-Sep-15	EVB Basement - Mezz Slab & Beam (Lv -1.4) - (Falsework/Fwk) > Zone 1A											
0515-1200	EVB Basement - Mezz Slab & Beam (Lv -1.4) - (Reb. Fix) > Zone 1A	6	16-Sep-15 A	17-Sep-15	EVB Basement - Mezz Slab & Beam (Lv -1.4) - (Reb. Fix)											
0515-1220	EVB Basement - Mezz Slab & Beam (Lv -1.4) - (Conc) > Zone 1A	2	18-Sep-15	19-Sep-15	EVB Basement - Mezz Slab & Beam (Lv -1.4) - (C											
0515-1240	EVB Basement - Col/Partition Wall (Reb. Fix) > Zone 2A: GL1-6/A-D (ind ST-04)	14	18-Sep-15	06-Oct-15												
0515-1260	EVB Basement - Col/Partition Wall (Fwk) > Zone 2A to Roof Soffit	14	03-Oct-15	19-Oct-15												
0515-1280	EVB Basement - Col/Partition Wall (Conc) > Zone 2A to Roof Soffit	2	20-Oct-15	22-Oct-15												
0515-1300	EVB Basement - Mezz Slab & Beam (Lv +2.65) - (Falsework/Fwk) > Zone 2A	6	23-Oct-15	29-Oct-15												
0515-1320	EVB Basement - Mezz Slab & Beam (Lv +2.65) - (Reb. Fix) > Zone 2A	3	30-Oct-15	02-Nov-15												
0515-1340	EVB Basement - Mezz Slab & Beam (Lv +2.65) - (Conc) > Zone 2A	1	03-Nov-15	03-Nov-15												
0515-1360	EVB Basement - Col/Partition Wall (Reb. Fix) > Zone 3A: GL1-6/E-H	6	12-Aug-15 A	13-Oct-15												
0515-1380	EVB Basement - Col/Partition Wall (Fwk) > Zone 3A to Roof Soffit	8	17-Aug-15 A	29-Oct-15												
0515-1400	EVB Basement - Col/Partition Wall (Conc) > Zone 3A to Roof Soffit	2	28-Oct-15	29-Oct-15												
0515-1420	EVB Basement - Col/Partition Wall (Reb. Fix) > Zone 4A: GL1-6/H-K	6	06-Aug-15 A	01-Sep-15	EVB Basement - Col/Partition Wall (Reb. Fix) > Zone 4A: GL1-6/H-K											
0515-1440	EVB Basement - Col/Partition Wall (Fwk) > Zone 4A to Roof Soffit	9	12-Aug-15 A	08-Sep-15	EVB Basement - Col/Partition Wall (Fwk) > Zone 4A to Roof Soffit											
0515-1460	EVB Basement - Col/Partition Wall (Conc) > Zone 4A to Roof Soffit	2	09-Sep-15	10-Sep-15	EVB Basement - Col/Partition Wall (Conc) > Zone 4A to Roof Soffit											
0515-1480	EVB Basement - Col/Partition Wall (Reb. Fix) > Zone 5A: GL1-6/K-O (ind ST-03)	3	07-Jul-15 A	22-Aug-15	EVB Basement - Col/Partition Wall (Reb. Fix) > Zone 5A: GL1-6/K-O (ind ST-03)											
0515-1500	EVB Basement - Col/Partition Wall (Fwk) > Zone 5A to Roof Soffit	5	11-Jul-15 A	25-Aug-15	EVB Basement - Col/Partition Wall (Fwk) > Zone 5A to Roof Soffit											
0515-1520	EVB Basement - Col/Partition Wall (Conc) > Zone 5A to Roof Soffit	1	30-Jul-15 A	26-Aug-15	EVB Basement - Col/Partition Wall (Conc) > Zone 5A to Roof Soffit											
0515-1540	EVB Basement - Roof Slab (Falsework/Fwk) > Zone 5B: GL1-6/K-O	21	08-Sep-15	03-Oct-15												
0515-1560	EVB Basement - Roof Slab (Reb Fix) > Zone 5B: GL1-6/K-O	14	02-Oct-15	17-Oct-15												
0515-1580	EVB Basement - Roof Slab (Conc) > Zone 5B: GL1-6/K-O	2	19-Oct-15	20-Oct-15												
0515-1600	EVB Basement - Roof Slab (Falsework/Fwk) > Zone 4B: GL1-6/H-K	21	05-Oct-15	29-Oct-15												
0515-1620	EVB Basement - Roof Slab (Reb Fix) > Zone 4B: GL1-6/H-K	14	28-Oct-15	12-Nov-15												
0515-1640	EVB Basement - Roof Slab (Conc) > Zone 4B: GL1-6/H-K	2	13-Nov-15	14-Nov-15												
0515-1660	EVB Basement - Roof Slab (Falsework/Fwk) > Zone 3B: GL1-6/E-H	21	30-Oct-15	23-Nov-15												
<b>05.2 - Cut &amp; Cover Tunnel Ch 4932-5149</b>																
<b>05.2.5 - Road &amp; Miscellaneous Works</b>																
0525-1240	Remedial Works - Bay 9 OHVD - WestBound	0	26-Jul-15 A	31-Jul-15 A	y 9 OHVD - WestBound											
0525-1260	Remedial Works - Concrete Repair Works / Trim overbreak Concrete Etc,Honeycoms	0	09-Mar-15 A	31-Jul-15 A	crete Repair Works / Trim overbreak Concrete Etc,Honeycoms/laitance, etc.											
0525-1280	Remedial Works - Sealing off Water Leakage at D-Wall	0	01-Jun-15 A	31-Jul-15 A	aling off Water Leakage at D-Wall											
<b>06 - SECTION 3 OF THE WORKS</b>																
<b>06.1 - Westbound - Pier 29-34</b>																
0610-1380	Construct W/B Bridge Pier 29 > Pile Cap	0	11-Jul-15 A	17-Aug-15 A	Construct W/B Bridge Pier 29 > Pile Cap											
0610-1400	Construct W/B Bridge Pier 29 > Column	5	18-Aug-15 A	25-Aug-15	Construct W/B Bridge Pier 29 > Column											
0610-1420	Construct W/B Bridge Pier 29 > Rebar Fixing - Crosshead	10	26-Aug-15	05-Sep-15	Construct W/B Bridge Pier 29 > Rebar Fixing - Crosshead											
0610-1440	Construct W/B Bridge Pier 29 > Formworks + Concreting - Crosshead	4	07-Sep-15	10-Sep-15	Construct W/B Bridge Pier 29 > Formworks + Concreting - Crosshead											
0610-1460	Construct W/B Bridge Pier 29 > Bearing	4	11-Sep-15	15-Sep-15	Construct W/B Bridge Pier 29 > Bearing											
0610-1480	Construct W/B Bridge Pier 30 > Pile Cap	0	06-Jul-15 A	01-Aug-15 A	dge Pier 30 > Pile Cap											

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme ( 20 Aug to 19 Nov 2015 )**

Activity ID	Activity Name	Remaining Duration	Start	Finish	2015											
					August				September				October			
					09	16	23	30	06	13	20	27				
0610-1500	Construct W/B Bridge Pier 30 > Column	0	02-Aug-15 A	10-Aug-15 A	Construct W/B Bridge Pier 30 > Column											
0610-1520	Construct W/B Bridge Pier 30 > Rebar Fixing - Crosshead	9	19-Aug-15 A	29-Aug-15	Construct W/B Bridge Pier 30 > Rebar Fixing - Crosshead											
0610-1540	Construct W/B Bridge Pier 30 > Formworks + Concreting - Crosshead	4	31-Aug-15	03-Sep-15	Construct W/B Bridge Pier 30 > Formworks + Concreting - Crosshead											
0610-1560	Construct W/B Bridge Pier 30 > Bearing	6	04-Sep-15	10-Sep-15	Construct W/B Bridge Pier 30 > Bearing											
0610-1580	Construct W/B Bridge Pier 31 > Pile Cap	0	08-Jul-15 A	08-Aug-15 A	Construct W/B Bridge Pier 31 > Pile Cap											
0610-1600	Construct W/B Bridge Pier 31 > Column	0	09-Aug-15 A	18-Aug-15 A	Construct W/B Bridge Pier 31 > Column											
0610-1620	Construct W/B Bridge Pier 31 > Rebar Fixing - Crosshead	9	19-Aug-15 A	29-Aug-15	Construct W/B Bridge Pier 31 > Rebar Fixing - Crosshead											
0610-1640	Construct W/B Bridge Pier 31 > Formworks + Concreting - Crosshead	4	31-Aug-15	03-Sep-15	Construct W/B Bridge Pier 31 > Formworks + Concreting - Crosshead											
0610-1660	Construct W/B Bridge Pier 31 > Bearing	5	04-Sep-15	09-Sep-15	Construct W/B Bridge Pier 31 > Bearing											
0610-1680	Construct W/B Bridge Pier 32 > Pile Cap	0	14-Jul-15 A	01-Aug-15 A	Construct W/B Bridge Pier 32 > Pile Cap											
0610-1700	Construct W/B Bridge Pier 32 > Column	0	02-Aug-15 A	14-Aug-15 A	Construct W/B Bridge Pier 32 > Column											
0610-1720	Construct W/B Bridge Pier 32 > Rebar Fixing - Crosshead	10	19-Aug-15 A	31-Aug-15	Construct W/B Bridge Pier 32 > Rebar Fixing - Crosshead											
0610-1740	Construct W/B Bridge Pier 32 > Formworks + Concreting - Crosshead	4	01-Sep-15	04-Sep-15	Construct W/B Bridge Pier 32 > Formworks + Concreting - Crosshead											
0610-1760	Construct W/B Bridge Pier 32 > Bearing	5	05-Sep-15	10-Sep-15	Construct W/B Bridge Pier 32 > Bearing											
0610-1780	Construct W/B Bridge Pier 33 > Pile Cap	0	28-Jul-15 A	10-Aug-15 A	Construct W/B Bridge Pier 33 > Pile Cap											
0610-1800	Construct W/B Bridge Pier 33 > Column	0	11-Aug-15 A	14-Aug-15 A	Construct W/B Bridge Pier 33 > Column											
0610-1820	Construct W/B Bridge Pier 33 > Rebar Fixing - Crosshead	10	20-Aug-15	31-Aug-15	Construct W/B Bridge Pier 33 > Rebar Fixing - Crosshead											
0610-1840	Construct W/B Bridge Pier 33 > Formworks + Concreting - Crosshead	4	01-Sep-15	04-Sep-15	Construct W/B Bridge Pier 33 > Formworks + Concreting - Crosshead											
0610-1860	Construct W/B Bridge Pier 33 > Bearing	5	05-Sep-15	10-Sep-15	Construct W/B Bridge Pier 33 > Bearing											
0610-1880	W/B Bridge Pier 34 - Tie Beam > Breaking + Excav + Blinding	8	12-Nov-15	20-Nov-15												
0610-1920	Construct W/B Bridge Pier 34 Drilling of Starter Bars for Pier/Column	14	12-Nov-15	27-Nov-15												
<b>06.3 - Admin Building</b>																
0630-1100	Grd. Beam - (GL > K-N) - Removal of Existing Sheet Piles	6	20-Aug-15	26-Aug-15	Grd. Beam - (GL > K-N) - Removal of Existing Sheet Piles											
0630-1101	Grd. Beam - (GL > K-N) - Excavate to formation level + Blinding Layer Casting	5	22-Aug-15	27-Aug-15	Grd. Beam - (GL > K-N) - Excavate to formation level + Blinding Layer Casting											
0630-1120	Grd. Beam - (GL > K-N) - Install Capping Plate	4	28-Aug-15	01-Sep-15	Grd. Beam - (GL > K-N) - Install Capping Plate											
0630-1140	Grd. Beam - (GL > K-N) - Rebar Fixing for Ground Beam	7	31-Aug-15	07-Sep-15	Grd. Beam - (GL > K-N) - Rebar Fixing for Ground Beam											
0630-1160	Grd. Beam - (GL > K-N) - Erect Formworks for Ground Beam	4	05-Sep-15	09-Sep-15	Grd. Beam - (GL > K-N) - Erect Formworks for Ground Beam											
0630-1180	Grd. Beam - (GL > K-N) - Cast Concrete for Ground Beam	1	10-Sep-15	10-Sep-15	Grd. Beam - (GL > K-N) - Cast Concrete for Ground Beam											
0630-1200	Grd. Beam - (GL > K-N) - Formworks Removal	1	11-Sep-15	11-Sep-15	Grd. Beam - (GL > K-N) - Formworks Removal											
0630-1600	Grd. Beam - (GL > D-G) - Removal of Existing Sheet Piles	1	10-Aug-15 A	20-Aug-15	Grd. Beam - (GL > D-G) - Removal of Existing Sheet Piles											
0630-1620	Grd. Beam - (GL > D-G) - Excavate to formation level + Blinding Layer Casting	5	21-Aug-15	26-Aug-15	Grd. Beam - (GL > D-G) - Excavate to formation level + Blinding Layer Casting											
0630-1640	Grd. Beam - (GL > D-G) - Install Capping Plate	4	26-Aug-15	29-Aug-15	Grd. Beam - (GL > D-G) - Install Capping Plate											
0630-1660	Grd. Beam - (GL > D-G) - Rebar Fixing for Ground Beam	7	28-Aug-15	04-Sep-15	Grd. Beam - (GL > D-G) - Rebar Fixing for Ground Beam											
0630-1700	Grd. Beam - (GL > D-G) - Erect Formworks for Ground Beam	4	05-Sep-15	09-Sep-15	Grd. Beam - (GL > D-G) - Erect Formworks for Ground Beam											
0630-1720	Grd. Beam - (GL > D-G) - Cast Concrete for Ground Beam	1	10-Sep-15	10-Sep-15	Grd. Beam - (GL > D-G) - Cast Concrete for Ground Beam											
0630-1740	Grd. Beam - (GL > D-G) - Formworks Removal	1	11-Sep-15	11-Sep-15	Grd. Beam - (GL > D-G) - Formworks Removal											
0630-2020	Grd. Beam - (GL > B-D) - Removal of Existing Sheet Piles	1	18-Aug-15 A	20-Aug-15	Grd. Beam - (GL > B-D) - Removal of Existing Sheet Piles											
0630-2021	Grd. Beam - (GL > B-D) - Excavate to formation level + Blinding Layer Casting	6	20-Aug-15	26-Aug-15	Grd. Beam - (GL > B-D) - Excavate to formation level + Blinding Layer Casting											
0630-2040	Grd. Beam - (GL > B-D) - Install Capping Plate	4	27-Aug-15	31-Aug-15	Grd. Beam - (GL > B-D) - Install Capping Plate											
0630-2080	Grd. Beam - (GL > B-D) - Rebar Fixing for Ground Beam	7	02-Sep-15	09-Sep-15	Grd. Beam - (GL > B-D) - Rebar Fixing for Ground Beam											
0630-2100	Grd. Beam - (GL > B-D) - Erect Formworks for Ground Beam	4	09-Sep-15	12-Sep-15	Grd. Beam - (GL > B-D) - Erect Formworks for Ground Beam											
0630-2120	Grd. Beam - (GL > B-D) - Cast Concrete for Ground Beam	1	14-Sep-15	14-Sep-15	Grd. Beam - (GL > B-D) - Cast Concrete for Ground Beam											
0630-2140	Grd. Beam - (GL > B-D) - Formworks Removal	1	15-Sep-15	15-Sep-15	Grd. Beam - (GL > B-D) - Formworks Removal											
A1000	Construction of pile cap for PC21	15	22-Oct-15	07-Nov-15												
A1010	Construction of pile cap for PC22	15	30-Oct-15	16-Nov-15												
A1020	Install underground drainage at Portion VB	12	27-Aug-15	09-Sep-15	Install underground drainage at Portion VB											
<b>08 - SECTION 5 WORK</b>																
<b>08.1 - Retaining Wall 'F' Substructure</b>																
0810-1640	Retaining Wall F > Pile Testing & prep for Caps Const	5	02-Oct-15*	07-Oct-15												
0810-1650	Retaining Wall F > Temp Excav Support/Open cut Excav works	21	08-Oct-15*	02-Nov-15												
0810-1660	Retaining Wall F > Excavation Works for Pile caps	25	19-Oct-15	17-Nov-15												
0810-1670	Construction of pile cap for Retaining Wall F @ C4-13	15	22-Oct-15	07-Nov-15												
0810-1680	Construction of pile cap for Retaining Wall F @ C4-14/C15-11	15	31-Oct-15	17-Nov-15												
0810-1700	Construction of pile cap for Retaining Wall F @ C5-12	15	10-Nov-15	26-Nov-15												

- Remaining Level of Effort
  - Actual Level of Effort
  - Actual Work
  - Remaining Work
  - Critical Remaining Work
- ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme ( 20 Aug to 19 Nov 2015 )**

Activity ID	Activity Name	Remaining Duration	Start	Finish	2015											
					August				September				October			
					09	16	23	30	06	13	20	27				
<b>09 - SECTION 6 OF THE WORKS</b>																
<b>09.2 - Westbound - Pier 26-27</b>																
0920-1080	Pier 27 Prepare C.J. and Modify Tie Beam	18	20-Aug-15	09-Sep-15	Pier 27 Prepare C.J. and Modify Tie Beam											
0920-1100	Pier 27 Construct Pier/Column	18	10-Sep-15	02-Oct-15	Pier 27 Construct Pier/Column											
0920-1120	Pier 27 Construct Crosshead	24	03-Oct-15	31-Oct-15	Pier 27 Construct Crosshead											
0920-1140	Pier 27 Install Bearing	9	02-Nov-15	11-Nov-15	Pier 27 Install Bearing											
0920-1160	Pier 26 Prepare C.J. + Drill in Re-bar + Modify Pilecap	18	20-Aug-15	09-Sep-15	Pier 26 Prepare C.J. + Drill in Re-bar + Modify Pilecap											
0920-1180	Pier 26 Construct Pier/Column	18	10-Sep-15	02-Oct-15	Pier 26 Construct Pier/Column											
0920-1200	Pier 26 Construct Crosshead	24	03-Oct-15	31-Oct-15	Pier 26 Construct Crosshead											
0920-1220	Pier 26 Install Bearing	9	02-Nov-15	11-Nov-15	Pier 26 Install Bearing											
<b>10 - SECTION X OF THE WORKS</b>																
<b>10.4 - Bridge Deck Demolition</b>																
<b>10.4.1 - Existing W/B Bridge (Part 1)</b>																
10410-1320	Excavate + Demolish W/B Bridge Pier 33 > Pile Cap	0	14-Jul-15 A	27-Jul-15 A	33 > Pile Cap											
10410-1440	Demolish W/B Bridge Pier 27 > Column > by Crane C	0	19-Jul-15 A	23-Jul-15 A	Demolish W/B Bridge Pier 27 > Column > by Crane C											
10410-1480	Demolish W/B Bridge Deck Pier 25-26 (7 beams) > by Crane B & C	0	23-Jul-15 A	25-Jul-15 A	Demolish W/B Bridge Deck Pier 25-26 (7 beams) > by Crane B & C											
10410-1500	Demolish W/B Bridge Pier 26 > Column > by Crane C	0	25-Jul-15 A	30-Jul-15 A	Demolish W/B Bridge Pier 26 > Column > by Crane C											
10410-1520	Saw Cutting W/B Bridge Deck Pier 24-25	0	30-Jul-15 A	01-Aug-15 A	Saw Cutting W/B Bridge Deck Pier 24-25											
10410-1540	Demolish W/B Bridge Deck Pier 24-25 (7 beams) > by Crane B & C	0	31-Jul-15 A	03-Aug-15 A	Demolish W/B Bridge Deck Pier 24-25 (7 beams) > by Crane B & C											
10410-1560	Demolish W/B Bridge Pier 25 > Column > by Crane C	0	03-Aug-15 A	06-Aug-15 A	Demolish W/B Bridge Pier 25 > Column > by Crane C											
10410-1580	Saw Cutting W/B Bridge Deck Pier 23-24	0	04-Aug-15 A	07-Aug-15 A	Saw Cutting W/B Bridge Deck Pier 23-24											
10410-1600	Demolish W/B Bridge Deck Pier 23-24 (7 beams) > by Crane B & C	0	06-Aug-15 A	10-Aug-15 A	Demolish W/B Bridge Deck Pier 23-24 (7 beams) > by Crane B & C											
10410-1620	Demolish W/B Bridge Pier 24 > Column > by Crane C	0	10-Aug-15 A	15-Aug-15 A	Demolish W/B Bridge Pier 24 > Column > by Crane C											
10410-1640	Saw Cutting W/B Bridge Deck Pier 22-23	0	13-Aug-15 A	16-Aug-15 A	Saw Cutting W/B Bridge Deck Pier 22-23											
10410-1660	Demolish W/B Bridge Deck Pier 22-23 (7 beams) > by Crane B & C	0	15-Aug-15 A	19-Aug-15 A	Demolish W/B Bridge Deck Pier 22-23 (7 beams) > by Crane B & C											
10410-1680	Demolish W/B Bridge Pier 23 > Column > by Crane C	5	20-Aug-15	25-Aug-15	Demolish W/B Bridge Pier 23 > Column > by Crane C											
10410-1700	Saw Cutting W/B Bridge Deck Pier 21-22	3	19-Aug-15 A	22-Aug-15	Saw Cutting W/B Bridge Deck Pier 21-22											
10410-1701	Dem. W/B Bridge Deck Pier 21-22 (1 beam) w/ time constraint start up to 4Pm > by C	1	24-Aug-15	24-Aug-15	Dem. W/B Bridge Deck Pier 21-22 (1 beam) w/ time constraint start up to 4Pm > by Crane B & C											
10410-1720	Demolish W/B Bridge Deck Pier 21-22 (5 beams) > by Crane B & C	3	25-Aug-15	27-Aug-15	Demolish W/B Bridge Deck Pier 21-22 (5 beams) > by Crane B & C											
10410-1740	Demolish W/B Bridge Pier 22 > Column > by Crane C	5	28-Aug-15	02-Sep-15	Demolish W/B Bridge Pier 22 > Column > by Crane C											
10410-1741	Saw Cutting W/B Bridge Deck Pier 20-21	2	28-Aug-15	29-Aug-15	Saw Cutting W/B Bridge Deck Pier 20-21											
10410-1742	Dem. W/B Bridge Deck Pier 20-21 (1 beam) w/ time constraint start up to 4Pm > by C	2	31-Aug-15	01-Sep-15	Dem. W/B Bridge Deck Pier 20-21 (1 beam) w/ time constraint start up to 4Pm > by Crane B & C											
10410-1743	Demolish W/B Bridge Deck Pier 20-21 (2 beams) > by Crane B & C	1	02-Sep-15	02-Sep-15	Demolish W/B Bridge Deck Pier 20-21 (2 beams) > by Crane B & C											
10410-1743.1	Cutting of W/B Bridge Crosshead Wing at Pier 21 for Modification	2	03-Sep-15	04-Sep-15	Cutting of W/B Bridge Crosshead Wing at Pier 21 for Modification											
10410-1744	Demolish W/B Bridge Deck Pier 19-20 (2 beams) > Insatall Scaffoldings to Support B	5	28-Aug-15	02-Sep-15	Demolish W/B Bridge Deck Pier 19-20 (2 beams) > Insatall Scaffoldings to Support Beams											
10410-1745	Saw Cutting W/B Bridge Deck Pier 19-20 @ 2 Beams into 8Pcs(1x4X2)	4	03-Sep-15	07-Sep-15	Saw Cutting W/B Bridge Deck Pier 19-20 @ 2 Beams into 8Pcs(1x4X2)											
10410-1746	Dem. W/B Bridge Deck Pier 19-20 (1 beam) w/ time constraint start up to 4Pm > by C	2	05-Sep-15	07-Sep-15	Dem. W/B Bridge Deck Pier 19-20 (1 beam) w/ time constraint start up to 4Pm > by Crane B											
10410-1747	Demolish W/B Bridge Deck Pier 19-20 (1 beam) > by Crane B	1	08-Sep-15	08-Sep-15	Demolish W/B Bridge Deck Pier 19-20 (1 beam) > by Crane B											
10410-1747.1	Cutting of W/B Bridge Crosshead Wing at Pier 20 for Modification	2	09-Sep-15	10-Sep-15	Cutting of W/B Bridge Crosshead Wing at Pier 20 for Modification											
10410-1747.5	Demolish W/B Bridge Deck Pier 17-18 (2 beams) > Insatall Scaffoldings to Support B	5	02-Sep-15	07-Sep-15	Demolish W/B Bridge Deck Pier 17-18 (2 beams) > Insatall Scaffoldings to Support Beams											
10410-1748	Saw Cutting W/B Bridge Deck Pier 17-18 @ 2 Beams into 8Pcs(1x4X2)	4	08-Sep-15	11-Sep-15	Saw Cutting W/B Bridge Deck Pier 17-18 @ 2 Beams into 8Pcs(1x4X2)											
10410-1749	Dem. W/B Bridge Deck Pier 17-18 (1 beam) > by Crane B	1	11-Sep-15	11-Sep-15	Dem. W/B Bridge Deck Pier 17-18 (1 beam) > by Crane B											
10410-1750	Demolish W/B Bridge Deck Pier 17-18 (1 beam) > by Crane B	1	12-Sep-15	12-Sep-15	Demolish W/B Bridge Deck Pier 17-18 (1 beam) > by Crane B											
10410-1751	Demolish W/B Bridge Deck Pier 18-19 (2 beams) > Construct Footing for Shoring of f	5	24-Aug-15	28-Aug-15	Demolish W/B Bridge Deck Pier 18-19 (2 beams) > Construct Footing for Shoring of Beams											
10410-1752	Demolish W/B Bridge Deck Pier 18-19 (2 beams) > Install Shoring + Fixing to hold Be.	5	29-Aug-15	03-Sep-15	Demolish W/B Bridge Deck Pier 18-19 (2 beams) > Install Shoring + Fixing to hold Beams											
10410-1753	Demolish W/B Bridge Deck Pier 18-19 (2 beams) > Saw Cutting of Bridge Deck & Par	10	04-Sep-15	15-Sep-15	Demolish W/B Bridge Deck Pier 18-19 (2 beams) > Saw Cutting of Bridge Deck & Par											
10410-1754	Dem. W/B Bridge Deck Pier 18-19 (Half Beam-Eastside) w/ time constraint start at 4l	2	14-Sep-15	15-Sep-15	Dem. W/B Bridge Deck Pier 18-19 (Half Beam-Eastside) w/ time constraint start at 4l											
10410-1755	Demolish W/B Bridge Deck Pier 18-19 (Half Beam-Eastside) > by Crane D	1	16-Sep-15	16-Sep-15	Demolish W/B Bridge Deck Pier 18-19 (Half Beam-Eastside) > by Crane D											
10410-1756	Dem. W/B Bridge Deck Pier 18-19 (Half Beam-Westside) w/ time constraint start at 4	1	17-Sep-15	17-Sep-15	Dem. W/B Bridge Deck Pier 18-19 (Half Beam-Westside) w/ time constraint start at 4											
10410-1757	Demolish W/B Bridge Deck Pier 18-19 (Half Beam-Westside) > by Crane D	1	18-Sep-15	18-Sep-15	Demolish W/B Bridge Deck Pier 18-19 (Half Beam-Westside) > by Crane D											
10410-1760	Cutting of W/B Bridge Crosshead Wing at Pier 19 for Modification > by Crane D	2	17-Sep-15	18-Sep-15	Cutting of W/B Bridge Crosshead Wing at Pier 19 for Modification > by Crane D											
10410-1761	Cutting of W/B Bridge Crosshead Wing at Pier 18 for Modification > by Crane D	2	19-Sep-15	21-Sep-15	Cutting of W/B Bridge Crosshead Wing at Pier 18 for Modification > by Crane D											
10410-1762	Removal of Shoring	2	19-Sep-15	21-Sep-15	Removal of Shoring											
10410-1763	Removal of Temporary Footing	5	22-Sep-15	26-Sep-15	Removal of Temporary Footing											

- Remaining Level of Effort
  - Actual Level of Effort
  - Actual Work
  - Remaining Work
  - Critical Remaining Work
- ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme ( 20 Aug to 19 Nov 2015 )**

Activity ID	Activity Name	Remaining Duration	Start	Finish	2015											
					August				September				October			
					09	16	23	30	06	13	20	27				
10410-2180	Demolish Temp. W/B Bridge - Deck > Pier 42 to 43 (6 beams)	0	17-Jul-15 A	28-Jul-15 A	Demolish Temp. W/B Bridge - Deck > Pier 42 to 43 (6 beams)											
10410-2200	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 43	0	29-Jul-15 A	07-Aug-15 A	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 43											
10410-2220	Demolish Temp. W/B Bridge - Deck > Pier 41 to 42 (6 beams)	0	08-Aug-15 A	11-Aug-15 A	Demolish Temp. W/B Bridge - Deck > Pier 41 to 42 (6 beams)											
10410-2240	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 42	0	12-Aug-15 A	18-Aug-15 A	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 42											
10410-2260	Demolish Temp. W/B Bridge - Deck > Pier 40 to 41 (6 beams)	0	18-Aug-15 A	19-Aug-15 A	Demolish Temp. W/B Bridge - Deck > Pier 40 to 41 (6 beams)											
10410-2280	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 41	7	20-Aug-15	27-Aug-15	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 41											
10410-2300	Demolish Temp. W/B Bridge - Deck > Pier 39 to 40 (6 beams)	4	28-Aug-15	01-Sep-15	Demolish Temp. W/B Bridge - Deck > Pier 39 to 40 (6 beams)											
10410-2320	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 40	7	02-Sep-15	09-Sep-15	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 40											
10410-2340	Demolish Temp. W/B Bridge - Deck > Pier 38 to 39 (6 beams)	4	10-Sep-15	14-Sep-15	Demolish Temp. W/B Bridge - Deck > Pier 38 to 39 (6 beams)											
10410-2360	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 39	7	15-Sep-15	22-Sep-15	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 39											
10410-2380	Demolish Temp. W/B Bridge - Deck > Pier 37 to 38 (6 beams)	3	23-Sep-15	25-Sep-15	Demolish Temp. W/B Bridge - Deck > Pier 37 to 38 (6 beams)											
10410-2400	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 38	7	26-Sep-15	06-Oct-15	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 38											
10410-2420	Demolish Temp. W/B Bridge - Deck > Pier 36 to 37 (6 beams)	3	07-Oct-15	09-Oct-15	Demolish Temp. W/B Bridge - Deck > Pier 36 to 37 (6 beams)											
10410-2440	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 37	7	10-Oct-15	17-Oct-15	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 37											
10410-2460	Demolish Temp. W/B Bridge - Deck > Pier 35 to 36 (6 beams)	3	19-Oct-15	22-Oct-15	Demolish Temp. W/B Bridge - Deck > Pier 35 to 36 (6 beams)											
10410-2480	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 36	7	23-Oct-15	30-Oct-15	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 36											
10410-2500	Demolish Temp. W/B Bridge - Deck > Pier 34 to 35 (6 beams)	3	31-Oct-15	03-Nov-15	Demolish Temp. W/B Bridge - Deck > Pier 34 to 35 (6 beams)											
10410-2520	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 35 (by crane)	7	04-Nov-15	11-Nov-15	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 35 (by crane)											
10410-2540	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 34 (by crane)	7	04-Nov-15	11-Nov-15	Demolish Temp. W/B Bridge - Crosshead & Pier > Pier 34 (by crane)											
10410-3020	Pier 22 Erect Falsework at existing W/B Bridge prior to demolition	0	14-Aug-15 A	16-Aug-15 A	Pier 22 Erect Falsework at existing W/B Bridge prior to demolition											
<b>10.1 - E/B Bridges (Bridge D, E and F)</b>																
<b>10.1.1 - Marine Pier Construction</b>																
<b>Pier F01 to F02</b>																
1011-8600	F1B Pier/Column Construction	12	07-Oct-15	20-Oct-15												
1011-8620	F1B Crosshead Construction	18	22-Oct-15	11-Nov-15												
1011-8640	Bearing installation pier F1B & F2B	12	12-Nov-15	25-Nov-15												
<b>10.1.4 - Bridge E / Hing Fat Slip Road</b>																
<b>Bridge Construction</b>																
1014-1840	Construction (Pier E4 - Pier E2) > Construct Pile Cap at Pier E3	2	03-Aug-15 A	21-Aug-15	Construction (Pier E4 - Pier E2) > Construct Pile Cap at Pier E3											
1014-1860	Construction (Pier E4 - Pier E2) > Construct Pier E3	9	22-Aug-15	01-Sep-15	Construction (Pier E4 - Pier E2) > Construct Pier E3											
1014-1880	Construction (Pier E4 - Pier E2) > Construct Crosshead + Bearing at Pier E3	21	02-Sep-15	25-Sep-15	Construction (Pier E4 - Pier E2) > Construct Pier E3											
1014-1900	Construction (Pier E4 - Pier E2) > Modification of Crosshead + Bearing at Pier E4 & E	14	20-Aug-15	05-Sep-15	Construction (Pier E4 - Pier E2) > Modification of Crosshead + Bearing at Pier E4 & E2											
1014-1920	Construction (Pier E4 - Pier E2) > Erect 3nos Beams > Pier E3-E2	5	26-Sep-15	03-Oct-15												
1014-1940	Construction (Pier E4 - Pier E2) > Erect 3nos Beams > Pier E4-E3	5	05-Oct-15	09-Oct-15												
1014-1960	Construction (Pier E4 - Pier E2) > Erect Scaffolding + Platform + Pre-cast Planking >	7	10-Oct-15	17-Oct-15												
1014-1980	Construction (Pier E4 - Pier E2) > Rebar Fixing of Deck + Diaphragm + Concreting >	14	16-Oct-15	02-Nov-15												
1014-2000	Construction (Pier E4 - Pier E2) > Construct Parapet D1-E2	14	15-Oct-15	02-Nov-15												
1014-2020	Construction (Pier E4 - Pier E2) > Construct Parapet E2-E4	14	03-Nov-15	18-Nov-15												
1014-2040	Construction (Pier E4 - Pier E2) > Install Street Furniture/GullyEtc.	14	03-Nov-15	18-Nov-15												
1014-2060	Construction (Pier E4 - Pier E2) > Install MJ at Pier E2	7	09-Nov-15	16-Nov-15												
1014-2080	Construction (Pier E4 - Pier E2) > Install MJ at Pier E3 & E4	8	12-Nov-15	20-Nov-15												
1014-2100	Construction (Pier E4 - Pier E2) > Asphalt + Road Markings, Install Street Furniture/Si	4	21-Nov-15	25-Nov-15												
1014-2940	Bridge E (Pier 19 - D1) - Noise Barrier > Post + Panel	14	02-Nov-15	17-Nov-15												
1014-2960	Bridge E (Pier 19 - D1) - Green Panel Installation	2	18-Nov-15	20-Nov-15												
<b>10.2 - W/B Bridges (Bridge C and F)</b>																
<b>10.2.1 - Pier Construction</b>																
<b>Pier 38 to 43</b>																
1021-1820	Pier 38 (F3C) Prepare C.J. at Existing Pile Cap	11	07-Oct-15	19-Oct-15												
1021-1840	Pier 38 (F3C) Construct Pier/Column	18	20-Oct-15	10-Nov-15												
1021-1900	Pier 39 (F4C) Prepare C.J. at Existing Pile Cap	11	23-Sep-15	07-Oct-15												
1021-1920	Pier 39 (F4C) Construct Pier/Column	18	08-Oct-15	29-Oct-15												
1021-1940	Pier 39 (F4C) Construct Crosshead	24	30-Oct-15	26-Nov-15												
1021-1980	Pier 40 (F5C) Prepare C.J. at Existing Pile Cap	11	10-Sep-15	22-Sep-15	Pier 40 (F5C) Prepare C.J. at Existing											
1021-2000	Pier 40 (F5C) Construct Pier/Column	18	23-Sep-15	15-Oct-15												
1021-2020	Pier 40 (F5C) Construct Crosshead	24	16-Oct-15	13-Nov-15												
1021-2040	Pier 40 (F5C) Install Bearing	9	14-Nov-15	24-Nov-15												

- Remaining Level of Effort
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme ( 20 Aug to 19 Nov 2015 )**



Activity ID	Activity Name	Remaining Duration	Start	Finish	2015											
					August			September			October					
					09	16	23	30	06	13	20	27				
1022-1070.5	Bridge C4 Stitching between Pier 30 and 31	3	27-Nov-15	30-Nov-15												
1022-1451	Bridge C4 - Erect Pier Segment at Pier 31 (1 no) > By Crane	2	11-Sep-15	12-Sep-15												
1022-1452	Bridge C4 - Erect Pier Segment at Pier 32(2 nos) > By Crane	3	14-Sep-15	16-Sep-15												
1022-1453	Bridge C5 - Erect Pier Segment at Pier 33 (1 no) > By Crane	2	17-Sep-15	18-Sep-15												
1022-1454	Erect Temp. Lowering Support on Top of Pier Segment P33, 32 & 31 (design TBC)	15	19-Sep-15	08-Oct-15												
1022-1455	Move LG1 to Temp. Lowering Support at Pier 33-31 from Pier 34-35	4	09-Oct-15	13-Oct-15												
1022-1456	Modify LG1 at Pier 31,32 and 33 for Segment Erection at Pier 32-44	26	14-Oct-15	13-Nov-15												
1022-1457	Bridge C4 Erect T-Span Segment at Piers 31 by LG1 (12 nos)	11	14-Nov-15	26-Nov-15												
<b>10.6 - Tunnel Approach Ramp</b>																
<b>10.6.1 - Approach Ramp (Excluding Portion IIB)</b>																
<b>Bored Piles</b>																
1061-1120	Bored Piles Testing Approach Ramp (112 nos)	80	01-Jun-15 A	24-Nov-15												
1061-3980	Pre Bored H-Pile > Pile Ramp - BN14 A	10	20-Aug-15*	31-Aug-15												
1061-4000	Pre Bored H-Pile > Pile Ramp - BN14 B	14	25-Aug-15	09-Sep-15												
1061-4020	Pre Bored H-Pile > Pile Ramp - BN15 A	14	10-Sep-15*	25-Sep-15												
1061-4040	Pre Bored H-Pile > Pile Ramp - BN15 B	14	15-Sep-15	02-Oct-15												
1061-4060	Pre Bored H-Pile > Pile Ramp - BN16 A	14	19-Sep-15	07-Oct-15												
1061-4080	Pre Bored H-Pile > Pile Ramp - BN16 B	14	24-Sep-15	12-Oct-15												
1061-4100	Pre Bored H-Pile > Pile Ramp - BM07 A	14	30-Sep-15	16-Oct-15												
1061-4120	Pre Bored H-Pile > Pile Ramp - BM07 B	14	06-Oct-15	22-Oct-15												
1061-4140	Pre Bored H-Pile > Pile Ramp - BM08 A	14	10-Oct-15	27-Oct-15												
1061-4160	Pre Bored H-Pile > Pile Ramp - BM08 B	14	15-Oct-15	31-Oct-15												
1061-4180	Pre Bored H-Pile > Pile Ramp - BM06 A	14	20-Oct-15	05-Nov-15												
1061-4200	Pre Bored H-Pile > Pile Ramp - BM06 B	14	26-Oct-15	10-Nov-15												
1061-4220	Pre Bored H-Pile > Pile Ramp - BM05 A	14	30-Oct-15	14-Nov-15												
1061-4240	Pre Bored H-Pile > Pile Ramp - BM05 B	14	04-Nov-15	19-Nov-15												
1061-4260	Pre Bored H-Pile > Pile Ramp - BM04 A	14	09-Nov-15	24-Nov-15												
1061-4280	Pre Bored H-Pile > Pile Ramp - BM04 B	14	13-Nov-15	28-Nov-15												
<b>ELS</b>																
1061-1160	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D12 Northern	14	31-Aug-15*	15-Sep-15												
1061-1180	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D10 Northern	14	16-Sep-15	03-Oct-15												
1061-1200	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D10-D09 Northern	14	05-Oct-15	20-Oct-15												
1061-1220	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D09-D08 Northern	14	22-Oct-15	06-Nov-15												
1061-1240	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D08-D07 Northern	14	07-Nov-15	23-Nov-15												
1061-1280	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D12 Southern	14	31-Aug-15	15-Sep-15												
1061-1300	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D11-D10 Southern	14	16-Sep-15	03-Oct-15												
1061-1320	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D10-D09 Southern	14	05-Oct-15	20-Oct-15												
1061-1340	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D09-D08 Southern	14	22-Oct-15	06-Nov-15												
1061-1360	Drive Sheet Pile for Trough A & B (excl IIB) - Appr. Ramp > Pier D08-D07 Southern	14	07-Nov-15	23-Nov-15												
1061-1400	Install & Operate Dewatering System (excl IIB) - Appr. Ramp > Pier D06-D08	14	19-Oct-15	04-Nov-15												
1061-1420	Install & Operate Dewatering System (excl IIB) - Appr. Ramp > Pier D08-D10	14	05-Nov-15	20-Nov-15												
<b>Structure</b>																
1061-1860	Construct Retaining Wall E Pile Cap (7 nos)	28	31-Oct-15	02-Dec-15												
<b>10.7 - Section X - Miscellaneous Works</b>																
<b>10.7.1 - TTM Stages</b>																
1071-1240	TTM Stage 5 - TMLG Consultation and Endorsement	98	29-Jun-15 A	25-Nov-15												
1071-1260	TTM Stage 5 - TTM Enabling Works	1	26-Nov-15	26-Nov-15												
1071-1280	TTM Stage 5 - Hing Fat Slip Road Divert 1 Lane through Bridge From Pier E4 to Pier	0		26-Nov-15												
<b>10.7.2 - Oil Street/Watson Road (Portion III)</b>																
1072-1220	Drainage works - Manhole 1-49B, DN450 & Associate Gully Pipes > Portion VIIB > Watson Road	0	05-May-15 A	28-Jul-15 A												
1072-1240	Drainage works - Manhole 1-49, DN300 & Associate Gully Pipes > Portion VIIB > Watson Road	0	15-May-15 A	30-Jul-15 A												
1072-1260	Drainage works - Manhole 1-48B, DN450 & Associate Gully Pipes > Portion VIIB > Watson Road	0	31-Jul-15 A	03-Aug-15 A												
1072-1280	Drainage works - Road Reinstatement > Portion VIIB > Watson Road	0	04-Aug-15 A	08-Aug-15 A												

- Remaining Level of Effort
  - Actual Level of Effort
  - Actual Work
  - Remaining Work
  - Critical Remaining Work
- ◆ ◆ Milestone

**Contract HY/2009/19**  
**Three Months Rolling Programme ( 20 Aug to 19 Nov 2015 )**

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2
<b>HY/2009/15 - Works Programme Rev. M (DD:20-Sep-12)</b>													
<b>Works in East Ventilation Adit - Based on Alternative Method</b>													
<b>Reinstatement of Breakwater</b>													
S3_54840	Reinstatement works -west side	7d/wk-1	60d	21-Feb-14 08 A	30-Sep-14 18	-85d							
S3_60085	Reinstatement works east side	7d/wk-1	60d	31-May-14 08 A	30-Sep-14 18	-85d							
S3_54845	Completion of Section 3 (KD8) in EVA Area (Alternative Method)	7d/wk-2	0d		30-Sep-14 18	-86d							
<b>Works in TS1/TS2 - OHVD and Cable Trough/Maintenance Walkway</b>													
<b>TS2 - OHVD and Cable Trough/Maintenance Walkway</b>													
<b>OHVD Slab and Cable Trough Construction</b>													
S3_6210	TS2 - OHVD/ Cable trough	7d/wk-1	40d	20-May-14 08 A	30-Sep-14 18	-85d							
S3_6212	Completion of Section 3 - TS1/TS2 Area (below -6mpd) KD8)	7d/wk-2	0d		30-Sep-14 18	-86d							
<b>Works in TS4/ME4 Area (Portion 14A, 14B, 15, 23)</b>													
<b>TS4/ME4 - Removal of Temporary Reclamation</b>													
<b>Remaining Works at TZ6</b>													
<b>Stage 4 - Seawall and Reclamation at TZ6</b>													
A-2010	Installation of seawall blocks (Qty: 245 nos.)	7d/wk-2	6d	15-Sep-14 08 A	26-Sep-14 18	-332d							
A-2020	Soil Backfilling up to -2.45mPD (Qty:3,000 cu.m.)	7d/wk-2	2d	25-Sep-14 08	26-Sep-14 18	-332d							
A-2030	Utilities installation for Mined Tunnel	7d/wk-2	1d	27-Sep-14 08	27-Sep-14 18	-332d							
A-2040	Soil backfilling up to ground level (Qty:2,000 cu.m.)	7d/wk-2	2d	28-Sep-14 08	29-Sep-14 18	-332d							
A-2050	Site clearance	7d/wk-2	1d	30-Sep-14 08	30-Sep-14 18	-305d							
A-2060	Handover to MTR	7d/wk-2	0d		30-Sep-14 18	-305d							
<b>Removal of Temporary Reclamation at TS4/ME4</b>													
<b>Stage 5 (Zones A, D &amp; F - TS4-D33 to D-26, SCL2 &amp; ME4-D19 to D13)</b>													
A-3000	D-Wall horizontal cutting (Qty: 62 pcs.)	7d/wk-2	21d	29-Aug-14 08 A	23-Sep-14 18	-340d							
<b>Stage 6 (Zone C - P4, ME4-D12 to ME4-D16 &amp; P3)</b>													
A-3011	Marine removal of temporary reclamation and seawall blocks (Zones C )	7d/wk-2	21d	31-Aug-14 08 A	02-Oct-14 18	-353d							
A-3030	D-Wall vertical cutting (Qty: 15 pcs.)	7d/wk-2	4d	03-Oct-14 08	06-Oct-14 18	-353d							
A-3040	D-Wall horizontal cutting (Qty: 20 pcs.)	7d/wk-2	5d	06-Oct-14 08	10-Oct-14 18	-352d							

<ul style="list-style-type: none"> <li><span style="display: inline-block; width: 15px; height: 10px; background-color: #ccc; border: 1px solid black;"></span> Summary Bar</li> <li><span style="display: inline-block; width: 15px; height: 10px; background-color: #f00; border: 1px solid black;"></span> Actual Level of Effort</li> <li><span style="display: inline-block; width: 15px; height: 10px; background-color: #000; border: 1px solid black;"></span> Actual Work</li> <li><span style="display: inline-block; width: 15px; height: 10px; background-color: #900; border: 1px solid black;"></span> Remaining Work</li> <li><span style="display: inline-block; width: 15px; height: 10px; background-color: #f00; border: 1px solid black;"></span> Critical Remaining Work</li> <li><span style="display: inline-block; width: 10px; height: 10px; border: 1px solid black; border-radius: 50%;"></span> Milestone</li> </ul>	<p>1 of 18</p> <p><b>China State Construction Engineering (Hong Kong) Ltd</b></p> <p>Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)</p> <p><b>WORKS PROGRAMME REV. M</b></p>	<p>Prepared by William Caluza</p> <table border="1"> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> <tr> <td>26-Sep...</td> <td>1st submission</td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> </table>	Date	Revision	Checked	Approved	26-Sep...	1st submission											 <p><b>中國建築工程(香港)有限公司</b> CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.</p>
	Date	Revision	Checked	Approved															
26-Sep...	1st submission																		

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
<b>Stage 7 (Zones C &amp; E - ME4-D06 to D01, SCL1 &amp; TS4-D25)</b>															
A-4000	Marine removal of temporary reclamation and seawall blocks (Zones C & E)	7d/wk-2	18d	06-Sep-14 08 A	06-Oct-14 18	-353d									
A-3090	Hole coring (Qty: 44 nos)	7d/wk-2	9d	20-Sep-14 08*	28-Sep-14 18	-346d									
A-4010	D-Wall vertical cutting (Qty: 27pcs.)	7d/wk-2	7d	07-Oct-14 08	13-Oct-14 18	-353d									
A-4020	D-Wall horizontal cutting (Qty: 37 pcs.)	7d/wk-2	10d	11-Oct-14 08	20-Oct-14 18	-353d									
<b>Stage 9 (Zone I - TS4-D01 to TS4-D08)</b>															
A-3050	Remaining removal of temporary reclamation (Zone I)	7d/wk-2	28d	29-Aug-14 08 A	01-Oct-14 18	-342d									
A-3060	Hole coring (Qty: 25 nos)	7d/wk-2	5d	02-Oct-14 08	06-Oct-14 18	-342d									
A-3070	D-Wall vertical cutting (Qty: 14 pcs.)	7d/wk-2	3d	07-Oct-14 08	09-Oct-14 18	-342d									
A-3080	D-Wall horizontal cutting (Qty: 24 pcs.)	7d/wk-2	5d	21-Oct-14 08	25-Oct-14 18	-353d									
<b>Stage 8 (Zones G &amp; K - TS4-D24 to TS4-D15)</b>															
A-4040	Relocation of RHKYC floating pontoon	7d/wk-2	5d	22-Sep-14 08*	26-Sep-14 18	-338d									
A-4050	Hole coring (Qty: 27 nos)	7d/wk-2	6d	29-Sep-14 08	04-Oct-14 18	-346d									
A-4060	Marine removal of temporary reclamation and seawall blocks (Zone G & K)	7d/wk-2	14d	11-Oct-14 08	24-Oct-14 18	-352d									
A-4070	D-Wall vertical cutting (Qty: 18pcs.)	7d/wk-2	4d	25-Oct-14 08	28-Oct-14 18	-352d									
A-4080	D-Wall horizontal cutting (Qty: 25 pcs.)	7d/wk-2	7d	26-Oct-14 08	01-Nov-14 18	-352d									
<b>Stage 10 (Zone J - TS4-D09 to TS4-D14)</b>															
A-4090	Land removal of temporary reclamation (Zone J)	7d/wk-2	10d	07-Oct-14 08	16-Oct-14 18	-344d									
A-5000	Hole coring (Qty: 32 nos)	7d/wk-2	7d	17-Oct-14 08	23-Oct-14 18	-340d									
A-5010	Marine removal of temporary reclamation (Zone J)	7d/wk-2	7d	26-Oct-14 08	01-Nov-14 18	-353d									
A-5020	D-Wall vertical cutting (Qty: 20 pcs.)	7d/wk-2	5d	02-Nov-14 08	06-Nov-14 18	-353d									
A-5030	D-Wall horizontal cutting (Qty: 26 pcs.)	7d/wk-2	7d	04-Nov-14 08	10-Nov-14 18*	-353d									
<b>Stage 13 - Phase 3 Mooring</b>															
A-5050	Final trimming of sea bed level	7d/wk-2	4d	02-Nov-14 08	05-Nov-14 18	-347d									
A-5060	Phase 3 Mooring	7d/wk-2	6d	06-Nov-14 08	11-Nov-14 18	-347d									
A-5040	Reinstatement of existing seawall (Zones I & J)	7d/wk-2	7d	11-Nov-14 08	17-Nov-14 18	-353d									
<b>Stage 12 - Re-provisioning of Jetty</b>															
S6_5258	Provision of Mobile Crane (until permanent re-provision of Jetty is completed)	7d/wk-1	160d	20-Feb-14 08 A	30-Dec-14 18	-335d									
A-6010	BA8 submission and consent for commencement of superstructure	7d/wk-2	28d	20-Sep-14 08 A	16-Oct-14 18	-336d									

-  Summary Bar
-  Actual Level of Effort
-  Actual Work
-  Remaining Work
-  Critical Remaining Work
-  Milestone

2 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

**WORKS PROGRAMME REV. M**

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep...	1st submission		



**中國建築工程(香港)有限公司**  
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015					2016							
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3					
A-6012	Submission of performance report	7d/wk-2	1d	25-Oct-14 08*	25-Oct-14 18	-286d													
A-6020	Erection of working platform for jetty beams and reinstate the floating portoon	7d/wk-2	10d	02-Nov-14 08	11-Nov-14 18	-352d													
A-6040	BA10 submission for authorized signatory and subcontractor	7d/wk-2	1d	12-Nov-14 08	12-Nov-14 18	-304d													
A-6030	Jetty beams construction	7d/wk-2	14d	12-Nov-14 08	25-Nov-14 18	-352d													
A-6052	Construction of floating pontoon	7d/wk-2	14d	26-Nov-14 08	09-Dec-14 18	-331d													
A-6050	BA13 submission + 14-day cube test results	7d/wk-2	28d	26-Nov-14 08	23-Dec-14 18	-352d													
A-6060	E&M and accessories installation	7d/wk-2	7d	24-Dec-14 08	30-Dec-14 18	-352d													
A-6070	Handover to RHKYC	7d/wk-2	1d	31-Dec-14 08	31-Dec-14 18	-352d													
<b>Stage 11 - Construction of TZ4</b>																			
A-6080	South side - laying rockfill and levelling stone (Qty: 1,550 cu.m)	7d/wk-2	12d	24-Sep-14 08	05-Oct-14 18	-339d													
A-6090	South side - install seawall blocks (Qty: 255 nos.)	7d/wk-2	6d	06-Oct-14 08	11-Oct-14 18	-339d													
A-7000	South side - general fill (Qty: 2,000 cu.m.)	7d/wk-2	2d	12-Oct-14 08	13-Oct-14 18	-339d													
A-7010	North side - laying rockfill and levelling stone (Qty: 1,550 cu.m)	7d/wk-2	12d	21-Oct-14 08	01-Nov-14 18	-346d													
A-7020	North side - install seawall blocks (Qty: 255 nos.)	7d/wk-2	6d	02-Nov-14 08	07-Nov-14 18	-346d													
A-7030	North side - general fill (Qty:2,000 cu.m.)	7d/wk-2	2d	08-Nov-14 08	09-Nov-14 18	-346d													
A-7040	Handover to contract TS3/SR8	7d/wk-2	1d	10-Nov-14 08	10-Nov-14 18*	-346d													
<b>TS4/ME4, Removal of Temporary Reclamation</b>																			
S26875	Completion of Section 2 (With ME4 option) (KD7)	7d/wk-2	0d		17-Nov-14 18	-353d													
S26890	Completion of Section 7B (ME4) (KD13)	7d/wk-2	0d		17-Nov-14 18	-353d													
<b>TS4 - OHVD / Cable Trough</b>																			
S5_6185	TS4 (incl. TS4+) - OHVD Slab - Area C (access through temp. opening at TZ4)	7d/wk-1	36d	02-Jan-15 08*	06-Feb-15 18	195d													
S5_6190	TS4 (incl. TS4+) - Cable Trough (access through temp. opening at TZ4)	7d/wk-1	60d	07-Feb-15 08*	14-Apr-15 18	195d													
S5_59850	Completion of Section 5 - TS4/ME4 Area (KD10), below -20mPD	7d/wk-2	0d		02-Nov-15 18*	0d													
<b>Works in TPCWAE Area (Portion 20A, 20B)</b>																			
<b>Removal of Temporary Reclamation</b>																			
<b>Removal of Temporary Reclamation &amp; Form TZ5</b>																			
S87670	Remove general fill /sea wall block	7d/wk-1	24d	20-May-14 08A	08-Oct-14 18	-296d													
S87675	Diaphragm wall saw cutting (1st D Wall cut on 23 Jun 2014)	7d/wk-1	31d	03-Sep-14 08A	16-Oct-14 18	-306d													
S87755	Form TZ5	7d/wk-1	18d	25-Sep-14 08	14-Oct-14 18	-304d													

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

3 of 18

China State Construction Engineering (Hong Kong) Ltd  
 Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)  
**WORKS PROGRAMME REV. M**

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep...	1st submission		



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016								
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3					
S6785	Achievement of KD5	7d/wk-2	0d		16-Oct-14 18	-323d													
S6787	Complete Reinstatement of Vertical Seawall (near PRE Office)	7d/wk-2	0d		27-Oct-14 18	-322d													
<b>Reinstate Mucking Out Access Shaft "C"</b>																			
S67240	Start reinstatement works (after completion of TPCWAW OHVD works)	6d/wk	0d	28-Mar-16 08		-102d													
S67225	Cast slab opening at top of CCT West bound (access shaft)	6d/wk	18d	28-Mar-16 08	16-Apr-16 18	-102d													
S67230	Removal of vertical shaft and backfilling	6d/wk	48d	11-Apr-16 08	04-Jun-16 18	-102d													
S67235	Reinstatement of pavement	6d/wk	12d	30-May-16 08	11-Jun-16 18	-102d													
<b>TPCWAE - OHVD / Cable Trough</b>																			
S5_7405	TPCWAE - Cable Trough (access through temp. opening at TZ5 & Portion 19)	6d/wk	48d	04-Sep-15 08	02-Nov-15 18	0d													
S5_7400	TPCWAE - OHVD Slab AT Area A (access through temp. opening at TZ5 & Portion 19)	6d/wk	48d	04-Sep-15 08	02-Nov-15 18	0d													
S5_59840	Completion of Section 5 - TPCWAE Area (KD10), below -20mPD	7d/wk-2	0d		02-Nov-15 18*	0d													
<b>Works in TPCWAW Area</b>																			
<b>TPCWAW - Temporary Reclamation</b>																			
<b>Temporary Reclamation -</b>																			
S6_9440	TPCWAW - place levelling stone and tamping, South side	7d/wk-1	6d	15-Oct-14 08	20-Oct-14 18	-122d													
S6_9450	TPCWAW - place seawall block to +4 at South side (Qty: 569 nos. @ 50 nos/day)	7d/wk-1	12d	21-Oct-14 08	01-Nov-14 18	-122d													
S6_9465	TPCWAW - place levelling stone and tamping, North side	7d/wk-1	6d	02-Nov-14 08	07-Nov-14 18	-122d													
S6_9470	TPCWAW - place seawall blocks to +4 North side (Qty:672 nos @ 50 nos/day)	7d/wk-1	14d	08-Nov-14 08	21-Nov-14 18	-122d													
S6_9495	TPCWAW - General fill to +2 within the seawall	7d/wk-1	17d	15-Nov-14 08	01-Dec-14 18	-122d													
S6_9490	TPCWAW - place seawall blocks to +4 at the temporary opening	7d/wk-1	7d	02-Dec-14 08	08-Dec-14 18	-122d													
S6_9475	TPCWAW - Remaining General fill to +4 within the seawall	7d/wk-1	10d	09-Dec-14 08	18-Dec-14 18	-122d													
<b>TPCWAW - Diaphragm Wall</b>																			
<b>Diaphragm Wall</b>																			
S6_9385	Site investigation	7d/wk-1	49d	01-Dec-14 08	21-Jan-15 18	-113d													
S6_8960	Install guide wall	7d/wk-1	40d	17-Dec-14 08	28-Jan-15 18	-120d													
S6_8955	Curtain grout along proposed diaphragm wall	7d/wk-1	40d	19-Dec-14 08	30-Jan-15 18	-122d													
S6_9382	Set up bentonite silo/plants and equipments	7d/wk-1	30d	19-Dec-14 08	20-Jan-15 18	-112d													
S6_9345	Diaphragm wall construction (34 panels @ 3 panels/ week)	7d/wk-1	68d	30-Jan-15 08	14-Apr-15 18	-141d													
S6_9350	Install shear pins on diaphragm wall	7d/wk-1	40d	14-Mar-15 08	26-Apr-15 18	-133d													

-  Summary Bar
-  Actual Level of Effort
-  Actual Work
-  Remaining Work
-  Critical Remaining Work
-  Milestone

4 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
S6_9355	Install king posts	7d/wk-1	40d	14-Mar-15 08	26-Apr-15 18	-133d			■	■					
S6_8970	Diaphragm Wall Pile test	7d/wk-1	40d	20-Mar-15 08	03-May-15 18	-129d			■	■					
S6_9375	Carry out contact/fissure grouting	7d/wk-1	29d	21-Mar-15 08	22-Apr-15 18	-141d			■	■					
<b>TPCWAW- ELS Works</b>															
<b>ELS Works</b>															
S6_9360	Install dewatering wells and piezometers	7d/wk-1	20d	30-Mar-15 08	22-Apr-15 18	-141d			■	■					
S6_9365	Install inclinometers inside D-wall	7d/wk-1	20d	15-Apr-15 08	05-May-15 18	-141d			■	■					
S6_8975	Carry out pumping tests	7d/wk-1	12d	23-Apr-15 08	05-May-15 18	-141d			■	■					
S6_8980	1st Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	06-May-15 08	15-May-15 18	-141d			■	■					
S6_9260	Submit pumping test report	7d/wk-1	1d	06-May-15 08	06-May-15 18	-137d			■	■					
S6_8985	1st Layer - install lateral support	7d/wk-1	10d	16-May-15 08	26-May-15 18	-141d			■	■					
S6_8990	Install vibrating wire strain gauge	7d/wk-1	10d	16-May-15 08	26-May-15 18	-141d			■	■					
S6_8995	2nd Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	18-May-15 08	28-May-15 18	-141d			■	■					
S6_9000	2nd Layer - install lateral support	7d/wk-1	10d	29-May-15 08	07-Jun-15 18	-141d			■	■					
S6_9005	3rd Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	31-May-15 08	09-Jun-15 18	-141d			■	■					
S6_9010	3rd Layer - install lateral support	7d/wk-1	10d	10-Jun-15 08	19-Jun-15 18	-141d			■	■					
S6_9015	4th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	12-Jun-15 08	22-Jun-15 18	-141d			■	■					
S6_9020	4th Layer - install lateral support	7d/wk-1	10d	23-Jun-15 08	03-Jul-15 18	-141d			■	■					
S6_9025	5th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	25-Jun-15 08	05-Jul-15 18	-141d			■	■					
S6_9030	5th Layer - install lateral support	7d/wk-1	10d	27-Jun-15 08	07-Jul-15 18	-141d			■	■					
S6_9035	6th Layer - D Wall conc over break if any & Soft Excavation	7d/wk-1	10d	08-Jul-15 08	17-Jul-15 18	-141d			■	■					
S6_9040	6th Layer - install lateral support	7d/wk-1	10d	18-Jul-15 08	27-Jul-15 18	-69d			■	■					
<b>TPCWAW - ROCK EXCAVATION</b>															
S6_6180	Rock excavation to formation	7d/wk-1	112d	18-Jul-15 08	09-Nov-15 18	-141d			■	■					
S6_9370	Install tie back anchor to D- Walls (area on west side, near Portion 11)	7d/wk-1	25d	20-Jul-15 08	13-Aug-15 18	-69d			■	■					
S6_9415	Install tie back anchor to D- Walls (east area)	7d/wk-1	20d	20-Jul-15 08	08-Aug-15 18	-69d			■	■					
S6_9055	Provide Access to WDII Contractor for demolition of bulkhead at Portion 11	7d/wk-2	0d		10-Nov-15 18	-133d			◆	◆					
<b>TPCWAW- CCT RC Structure</b>															
<b>TPCWAW - CCT / OHVD</b>															

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

5 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING HONG KONG LTD.



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016							
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
A8705	SR8 Bench Excavation From West, CH 4065- 4075 = 10m	7d/wk-1a	20d	25-Sep-14 08	15-Oct-14 18	148d												
A8685	SR8 Bench Excavation From West, CH 4075- 4085 = 10m	7d/wk-1a	20d	16-Oct-14 08	04-Nov-14 18	148d												
A8680	SR8 Bench Excavation From West, CH 4085- 4095 = 10m	7d/wk-1a	20d	05-Nov-14 08	24-Nov-14 18	148d												
A8725	SR8 Bench Excavation From West, CH 4095- 4100 = 5m	7d/wk-1a	10d	25-Nov-14 08	04-Dec-14 18	148d												
<b>From East (TS4)</b>																		
<b>Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)</b>																		
A8495	SR8 Heading Excavation From East CH 4115- 4107 = 8m @2d/m	7d/wk-1a	16d	15-Sep-14 08 A	28-Sep-14 18	10d												
<b>Bench Excavation (1.5d/m, 20m separation with heading)</b>																		
A8455	SR8 Bench Excavation From East, CH 4147.5- 4135 = 12.5m	7d/wk-1a	19d	20-Sep-14 08	09-Oct-14 18	0d												
A8470	SR8 Bench Excavation From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	10-Oct-14 08	24-Oct-14 18	0d												
A8460	SR8 Bench Excavation From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	25-Oct-14 08	08-Nov-14 18	0d												
A8465	SR8 Bench Excavation From East, CH 4115- 4100 = 15m	7d/wk-1a	23d	09-Nov-14 08	01-Dec-14 18	0d												
<b>Tunnel Lining Works</b>																		
<b>From West - Base Slab (10m/bay, 10m separation with benching excavation)</b>																		
A8525	SR8, From West, CH 4015 - 4025 = 10m/bay, base slab	7d/wk-1a	10d	15-Sep-14 08 A	04-Oct-14 18	137d												
A8530	SR8, From West, CH 4025 - 4035 = 10m/bay, base slab	7d/wk-1a	10d	05-Oct-14 08	14-Oct-14 18	163d												
A8535	SR8, From West, CH 4035 - 4045 = 10m/bay, base slab	7d/wk-1a	8d	15-Oct-14 08	22-Oct-14 18	165d												
A8540	SR8, From West, CH 4045 - 4055 = 10m/bay, base slab	7d/wk-1a	8d	23-Oct-14 08	30-Oct-14 18	165d												
A8545	SR8, From West, CH 4055 - 4065 = 10m/bay, base slab	7d/wk-1a	8d	05-Nov-14 08	12-Nov-14 18	160d												
A8550	SR8, From West, CH 4065 - 4075 = 10m/bay, base slab	7d/wk-1a	8d	25-Nov-14 08	02-Dec-14 18	148d												
A8555	SR8, From West, CH 4075 - 4085 = 10m/bay, base slab	7d/wk-1a	8d	05-Dec-14 08	12-Dec-14 18	148d												
A8560	SR8, From West, CH 4085 - 4095 = 10m/bay, base slab	7d/wk-1a	8d	13-Dec-14 08	20-Dec-14 18	150d												
A8561	SR8, From West, CH 4095 - 4105 = 10m/bay, base slab	7d/wk-1a	8d	21-Dec-14 08	29-Dec-14 18	152d												
A8562	SR8, From West, CH 4105 - 4115 = 10m/bay, base slab	7d/wk-1a	8d	30-Dec-14 08	07-Jan-15 18	154d												
<b>From West - Lining (5m/bay, 10m separation with base slab)</b>																		
A8575	SR8, From West, CH 3995 - 4000 = 1bay, lining	7d/wk-1a	9d	20-Sep-14 08	28-Sep-14 18	0d												
A8580	SR8, From West, CH 4000 - 4005 = 1bay, lining	7d/wk-1a	9d	05-Oct-14 08	13-Oct-14 18	137d												
A8585	SR8, From West, CH 4005 - 4010 = 1bay, lining	7d/wk-1a	9d	14-Oct-14 08	22-Oct-14 18	137d												
A8590	SR8, From West, CH 4010 - 4015 = 1bay, lining	7d/wk-1a	9d	23-Oct-14 08	31-Oct-14 18	137d												

- Summary Bar
- ▬ Actual Level of Effort
- ▬ Actual Work
- ▬ Remaining Work
- ▬ Critical Remaining Work
- ◆ Milestone

China State Construction Engineering (Hong Kong) Ltd  
 Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)  
**WORKS PROGRAMME REV. M**

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep...	1st submission		



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016							
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
A8595	SR8, From West, CH 4015 - 4020 = 1bay, lining	7d/wk-1a	9d	01-Nov-14 08	09-Nov-14 18	137d												
A8600	SR8, From West, CH 4020 - 4025 = 1bay, lining	7d/wk-1a	9d	10-Nov-14 08	18-Nov-14 18	137d												
A8605	SR8, From West, CH 4025 - 4030 = 1bay, lining	7d/wk-1a	5d	19-Nov-14 08	23-Nov-14 18	137d												
A8610	SR8, From West, CH 4030 - 4035 = 1bay, lining	7d/wk-1a	5d	24-Nov-14 08	28-Nov-14 18	137d												
A8615	SR8, From West, CH 4035 - 4040 = 1bay, lining	7d/wk-1a	5d	29-Nov-14 08	03-Dec-14 18	137d												
A8620	SR8, From West, CH 4040 - 4045 = 1bay, lining	7d/wk-1a	5d	04-Dec-14 08	08-Dec-14 18	137d												
A8625	SR8, From West, CH 4045 - 4050 = 1bay, lining	7d/wk-1a	5d	09-Dec-14 08	13-Dec-14 18	137d												
A8630	SR8, From West, CH 4050 - 4055 = 1bay, lining	7d/wk-1a	5d	14-Dec-14 08	18-Dec-14 18	137d												
A8635	SR8, From West, CH 4055 - 4060 = 1bay, lining	7d/wk-1a	5d	19-Dec-14 08	23-Dec-14 18	137d												
A8640	SR8, From West, CH 4060 - 4065 = 1bay, lining	7d/wk-1a	5d	24-Dec-14 08	29-Dec-14 18	137d												
A8645	SR8, From West, CH 4065 - 4070 = 1bay, lining	7d/wk-1a	5d	30-Dec-14 08	04-Jan-15 18	137d												
A8647	SR8, From West, CH 4070 - 4075 = 1bay, lining	7d/wk-1a	5d	05-Jan-15 08	09-Jan-15 18	137d												
A8648	SR8, From West, CH 4075 - 4080 = 1bay, lining	7d/wk-1a	5d	10-Jan-15 08	14-Jan-15 18	137d												
A8649	SR8, From West, CH 4080 - 4085 = 1bay, lining	7d/wk-1a	5d	15-Jan-15 08	19-Jan-15 18	137d												
A8651	SR8, From West, CH 4085 - 4090 = 1bay, lining	7d/wk-1a	5d	20-Jan-15 08	24-Jan-15 18	137d												
A8652	SR8, From West, CH 4090 - 4095 = 1bay, lining	7d/wk-1a	5d	25-Jan-15 08	29-Jan-15 18	137d												
A8653	SR8, From West, CH 4095 - 4100 = 1bay, lining	7d/wk-1a	5d	30-Jan-15 08	03-Feb-15 18	137d												
A8654	SR8, From West, CH 4100 - 4105 = 1bay, lining	7d/wk-1a	5d	04-Feb-15 08	08-Feb-15 18	137d												
From East - Base Slab (10m/bay, 10m separation with benching excavation)																		
A9775	SR8 From East, CH 4149.5 - 4145 = 4.5m, base slab	7d/wk-1a	8d	02-Dec-14 08	09-Dec-14 18	0d												
A9780	SR8 From East, CH 4145 - 4135 = 10m/bay, base slab	7d/wk-1a	8d	10-Dec-14 08	17-Dec-14 18	0d												
A9785	SR8 From East, CH 4135 - 4125 = 10m/bay, base slab	7d/wk-1a	8d	18-Dec-14 08	26-Dec-14 18	8d												
A9786	SR8 From East, CH 4125 - 4115 = 10m/bay, base slab	7d/wk-1a	8d	27-Dec-14 08	04-Jan-15 18	10d												
From East - Lining (5m/bay, 10m separation with base slab)																		
A9820	From East, SR8 CH 4149.5 - 4145 = 4.5m, 1 bay, lining	7d/wk-1a	5d	18-Dec-14 08	22-Dec-14 18	0d												
A9815	From East, SR8 CH 4145 - 4140 = 1bay, lining	7d/wk-1a	5d	23-Dec-14 08	28-Dec-14 18	6d												
A9810	From East, SR8 CH 4140 - 4135 = 1bay, lining	7d/wk-1a	5d	29-Dec-14 08	03-Jan-15 18	6d												
A9805	From East, SR8 CH 4135 - 4130 = 1bay, lining	7d/wk-1a	5d	04-Jan-15 08	08-Jan-15 18	6d												

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

8 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2
A9870	From East, SR8 CH 4130 - 4125 = 1bay, lining	7d/wk-1a	5d	09-Jan-15 08	13-Jan-15 18	6d		■	From East, SR8 CH 4130 - 4125 = 1bay, lining				
A9800	From East, SR8 CH 4125 - 4120 = 1bay, lining	7d/wk-1a	5d	14-Jan-15 08	18-Jan-15 18	143d		■	From East, SR8 CH 4125 - 4120 = 1bay, lining				
A9860	From East, SR8 CH 4120 - 4115 = 1bay, lining	7d/wk-1a	5d	19-Jan-15 08	23-Jan-15 18	143d		■	From East, SR8 CH 4120 - 4115 = 1bay, lining				
A9855	From East, SR8 CH 4115 - 4110 = 1bay, lining	7d/wk-1a	5d	24-Jan-15 08	28-Jan-15 18	143d		■	From East, SR8 CH 4115 - 4110 = 1bay, lining				
A9850	From East, SR8 CH 4110 - 4105 = 1bay, lining	7d/wk-1a	5d	29-Jan-15 08	02-Feb-15 18	143d		■	From East, SR8 CH 4110 - 4105 = 1bay, lining				
<b>OHVD(10m/bay) / Utility Trough</b>													
A8570	SR8 Tunnel OHVD and utility trough =, 167= 17 bays @ 10m/bay @ 7d/bay	7d/wk-1a	120d	09-Feb-15 08	13-Jun-15 18	137d		■	SR8 Tunnel OHVD and utility trough =, 167= 17 bays @ 10m/bay @ 7d/bay				
<b>EB Outer Tunnel Excavation</b>													
<b>From West (TPCWAE)</b>													
<b>Outer Bench Excavation (1.5d - 2d/m, 20m separation with heading)</b>													
A9550	EB, Outer Bench From West, CH 4035- 4045 = 10m	7d/wk-1a	30d	07-Aug-14 08 A	20-Oct-14 18	135d	■	EB, Outer Bench From West, CH 4035- 4045 = 10m					
A9555	EB, Outer Bench From West, CH 4045- 4055 = 10m (2d/m)	7d/wk-1a	20d	20-Oct-14 08	08-Nov-14 18	135d	■	EB, Outer Bench From West, CH 4045- 4055 = 10m (2d/m)					
A9560	EB, Outer Bench From West, CH 4055- 4065 = 10m (2d/m)	7d/wk-1a	20d	09-Nov-14 08	28-Nov-14 18	135d	■	EB, Outer Bench From West, CH 4055- 4065 = 10m (2d/m)					
A9565	EB, Outer Bench From West, CH 4065- 4075 = 10m (2d/m)	7d/wk-1a	20d	29-Nov-14 08	18-Dec-14 18	135d	■	EB, Outer Bench From West, CH 4065- 4075 = 10m (2d/m)					
A9520	EB, Outer Bench From West, CH 4075- 4085 = 10m (2d/m)	7d/wk-1a	20d	19-Dec-14 08	09-Jan-15 18	135d	■	EB, Outer Bench From West, CH 4075- 4085 = 10m (2d/m)					
A9545	EB, Outer Bench From West, CH 4085- 4095 = 10m 1.5d/m)	7d/wk-1a	15d	10-Jan-15 08	24-Jan-15 18	135d	■	EB, Outer Bench From West, CH 4085- 4095 = 10m 1.5d/m)					
<b>From East (TS4)</b>													
<b>Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)</b>													
A9605	EB, Outer Bench From East, CH 4147.5 - 4145 = 2.5m	7d/wk-1a	30d	20-Oct-14 08*	18-Nov-14 18	120d	■	EB, Outer Bench From East, CH 4147.5 - 4145 = 2.5m					
A9610	EB, Outer Bench From East, CH 4145- 4135 = 10m (2d/m)	7d/wk-1a	20d	19-Nov-14 08	08-Dec-14 18	120d	■	EB, Outer Bench From East, CH 4145- 4135 = 10m (2d/m)					
A9615	EB, Outer Bench From East, CH 4135- 4125 = 10m (2d/m)	7d/wk-1a	20d	09-Dec-14 08	29-Dec-14 18	120d	■	EB, Outer Bench From East, CH 4135- 4125 = 10m (2d/m)					
A9620	EB, Outer Bench From East, CH 4125- 4115 = 10m (2d/m)	7d/wk-1a	20d	30-Dec-14 08	19-Jan-15 18	120d	■	EB, Outer Bench From East, CH 4125- 4115 = 10m (2d/m)					
A9625	EB, Outer Bench From East, CH 4115- 4105 = 10m (2d/m)	7d/wk-1a	20d	20-Jan-15 08	08-Feb-15 18	120d	■	EB, Outer Bench From East, CH 4115- 4105 = 10m (2d/m)					
A9630	EB, Outer Bench From East, CH 4105- 4095 = 10m (1.5d/m)	7d/wk-1a	15d	09-Feb-15 08	26-Feb-15 18	120d	■	EB, Outer Bench From East, CH 4105- 4095 = 10m (1.5d/m)					
<b>EB (Inner Tunnel Excavation + Lining)</b>													
<b>From West (TPCWAE)</b>													
<b>Inner Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)</b>													
A8805	EB, Inner Heading From West, CH 3992- 4005 = 13m @3d/m	7d/wk-1a	39d	29-Sep-14 08	07-Nov-14 18	0d	■	EB, Inner Heading From West, CH 3992- 4005 = 13m @3d/m					
A8815	EB, Inner Heading From West, CH 4005- 4015 = 10m @2d/m	7d/wk-1a	20d	08-Nov-14 08	27-Nov-14 18	0d	■	EB, Inner Heading From West, CH 4005- 4015 = 10m @2d/m					

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

9 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016				
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	
A8820	EB,Inner Heading From West , CH 4015- 4025 = 10m @2d/m	7d/wk-1a	20d	28-Nov-14 08	17-Dec-14 18	0d		■	■	■	■				
A8780	EB,Inner Heading From West, CH 4025- 4035 = 10m @2d/m	7d/wk-1a	20d	18-Dec-14 08	08-Jan-15 18	0d		■	■	■	■				
A8810	EB,Inner Heading From West , CH 4035- 4045 = 10m @2d/m	7d/wk-1a	20d	09-Jan-15 08	28-Jan-15 18	0d		■	■	■	■				
A8785	EB,Inner Heading From West , CH 4045- 4055 = 10m @2d/m	7d/wk-1a	20d	29-Jan-15 08	17-Feb-15 18	0d		■	■	■	■				
A8790	EB,Inner Heading From West, CH 4055- 4065 = 10m @ 2d/m	7d/wk-1a	20d	18-Feb-15 08	12-Mar-15 18	0d		■	■	■	■				
A8795	EB,Inner Heading From West , CH 4065- 4075 = 10m, @ 2d/m	7d/wk-1a	20d	13-Mar-15 08	01-Apr-15 18	0d		■	■	■	■				
A8800	EB,Inner Heading From West, CH 4075- 4085 = 10m @ 2d/m	7d/wk-1a	20d	02-Apr-15 08	22-Apr-15 18	0d		■	■	■	■				
A8825	EB,Inner Heading From West, CH 4085- 4095 = 10m @ 2d/m	7d/wk-1a	20d	23-Apr-15 08	13-May-15 18	0d		■	■	■	■				
<b>Inner Bench Excavation (1.5-2d/m, 20m separation with heading)</b>															
A8765	EB, Inner Bench From West, CH 3992-4005 = 13m (2d/m)	7d/wk-1a	26d	08-Nov-14 08	03-Dec-14 18	23d		■	■	■	■				
A8770	EB, Inner Bench From West,CH 4005- 4015 = 10m	7d/wk-1a	15d	18-Dec-14 08	03-Jan-15 18	9d		■	■	■	■				
A8775	EB, Inner Bench From West,CH 4015- 4025 = 10m	7d/wk-1a	15d	09-Jan-15 08	23-Jan-15 18	4d		■	■	■	■				
A8735	EB, Inner Bench From West,CH 4025- 4035 = 10m	7d/wk-1a	15d	29-Jan-15 08	12-Feb-15 18	14d		■	■	■	■				
A8740	EB, Inner Bench From West,CH 4035- 4045 = 10m	7d/wk-1a	15d	18-Feb-15 08	07-Mar-15 18	11d		■	■	■	■				
A8745	EB, Inner Bench From West,CH 4045- 4055 = 10m	7d/wk-1a	15d	13-Mar-15 08	27-Mar-15 18	6d		■	■	■	■				
A8750	EB, Inner Bench From West,CH 4055- 4065 = 10m	7d/wk-1a	15d	02-Apr-15 08	17-Apr-15 18	1d		■	■	■	■				
A8755	EB, Inner Bench From West,CH 4065- 4075 = 10m	7d/wk-1a	15d	18-Apr-15 08	03-May-15 18	1d		■	■	■	■				
A8760	EB, Inner Bench From West,CH 4075- 4085 = 10m	7d/wk-1a	15d	05-May-15 08	19-May-15 18	0d		■	■	■	■				
A8761	EB, Inner Bench From West,CH 4085- 4095 = 10m	7d/wk-1a	15d	20-May-15 08	03-Jun-15 18	0d		■	■	■	■				
<b>From East (TS4)</b>															
<b>Inner Heading Excavation (3d/m, 24h/day work shift, 7d/week, no work on statutory holiday)</b>															
A8835	EB,Inner Heading From East, CH 4147.5 to 4145 = 2.5m, @ 3d/m	7d/wk-1a	8d	06-Jan-15 08	13-Jan-15 18	0d		■	■	■	■				
A8850	EB,Inner Heading From East, CH 4145- 4135 = 10m, @ 3d/m	7d/wk-1a	30d	14-Jan-15 08	12-Feb-15 18	0d		■	■	■	■				
A8830	EB,Inner Heading From East, CH 4135- 4125 = 10m @2d/m	7d/wk-1a	20d	13-Feb-15 08	07-Mar-15 18	0d		■	■	■	■				
A8840	EB,Inner Heading From East, CH 4125- 4115 = 10m @2d/m	7d/wk-1a	20d	08-Mar-15 08	27-Mar-15 18	0d		■	■	■	■				
A9910	EB,Inner Heading From East, CH 4115- 4105 = 10m @2d/m	7d/wk-1a	20d	28-Mar-15 08	17-Apr-15 18	0d		■	■	■	■				
A8845	EB,Inner Heading From East, CH 4105- 4095 = 10m @2d/m	7d/wk-1a	20d	18-Apr-15 08	08-May-15 18	0d		■	■	■	■				
<b>Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)</b>															
A8860	EB,Inner Bench From East, CH 4147.5 - 4145 = 2.5m	7d/wk-1a	4d	08-Mar-15 08	11-Mar-15 18	11d		■	■	■	■				

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

10 of 18

**China State Construction Engineering (Hong Kong) Ltd**

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

**WORKS PROGRAMME REV. M**

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep...	1st submission		

**中國建築工程(香港)有限公司**

CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A8865	EB, Inner Bench From East, CH 4145- 4135 = 10m	7d/wk-1a	15d	12-Mar-15 08	26-Mar-15 18	11d			■ EB, Inner Bench From East, CH 4145- 4135 = 10m					
A8870	EB, Inner Bench From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	28-Mar-15 08	12-Apr-15 18	10d			■ EB, Inner Bench From East, CH 4135- 4125 = 10m					
A8855	EB, Inner Bench From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	18-Apr-15 08	03-May-15 18	5d			■ EB, Inner Bench From East, CH 4125- 4115 = 10m					
A8875	EB, Inner Bench From East, CH 4115- 4105 = 10m	7d/wk-1a	15d	09-May-15 08	23-May-15 18	0d			■ EB, Inner Bench From East, CH 4115- 4105 = 10m					
A9915	EB, Inner Bench From East, CH 4105- 4095 = 10m	7d/wk-1a	15d	24-May-15 08	08-Jun-15 18	0d			■ EB, Inner Bench From East, CH 4105- 4095 = 10m					
<b>Tunnel Lining Works</b>														
<b>From West Base Slab (10m/bay, 10m separation with benching excavation)</b>														
A8900	EB From West, Base Slab CH 3990 - 3995 = 1 bay	7d/wk-1a	10d	04-Dec-14 08	13-Dec-14 18	33d			■ EB From West, Base Slab CH 3990 - 3995 = 1 bay					
A8890	EB From West, Base Slab CH 3995 - 4005 = 10m/bay	7d/wk-1a	10d	04-Jan-15 08	13-Jan-15 18	14d			■ EB From West, Base Slab CH 3995 - 4005 = 10m/bay					
A8905	EB From West, Base Slab CH 4005 - 4015 = 10m/bay	7d/wk-1a	10d	24-Jan-15 08	02-Feb-15 18	4d			■ EB From West, Base Slab CH 4005 - 4015 = 10m/bay					
A8910	EB From West, Base Slab CH 4015 - 4025 = 10m/bay	7d/wk-1a	10d	13-Feb-15 08	25-Feb-15 18	14d			■ EB From West, Base Slab CH 4015 - 4025 = 10m/bay					
A8915	EB From West, Base Slab CH 4025 - 4035 = 10m/bay	7d/wk-1a	10d	08-Mar-15 08	17-Mar-15 18	12d			■ EB From West, Base Slab CH 4025 - 4035 = 10m/bay					
A8920	EB From West, Base Slab CH 4035 - 4045 = 10m/bay	7d/wk-1a	10d	28-Mar-15 08	07-Apr-15 18	8d			■ EB From West, Base Slab CH 4035 - 4045 = 10m/bay					
A8925	EB From West, Base Slab CH 4045 - 4055 = 10m/bay	7d/wk-1a	10d	18-Apr-15 08	27-Apr-15 18	4d			■ EB From West, Base Slab CH 4045 - 4055 = 10m/bay					
A8930	EB From West, Base Slab CH 4055 - 4065 = 10m/bay	7d/wk-1a	10d	04-May-15 08	13-May-15 18	5d			■ EB From West, Base Slab CH 4055 - 4065 = 10m/bay					
A8880	EB From West, Base Slab CH 4065 - 4075 = 10m/bay	7d/wk-1a	10d	20-May-15 08	29-May-15 18	5d			■ EB From West, Base Slab CH 4065 - 4075 = 10m/bay					
A8885	EB From West, Base Slab CH 4075 - 4085 = 10m/bay	7d/wk-1a	10d	04-Jun-15 08	13-Jun-15 18	0d			■ EB From West, Base Slab CH 4075 - 4085 = 10m/bay					
A8895	EB From West, Base Slab CH 4085 - 4095 = 10m/bay	7d/wk-1a	10d	14-Jun-15 08	24-Jun-15 18	0d			■ EB From West, Base Slab CH 4085 - 4095 = 10m/bay					
<b>From East Base Slab (10m/bay, 10m separation with benching excavation)</b>														
A9905	EB From East, Base Slab CH 4149.5 - 4145 = 4.5m	7d/wk-1a	10d	13-Apr-15 08	22-Apr-15 18	26d			■ EB From East, Base Slab CH 4149.5 - 4145 = 4.5m					
A9900	EB From East, Base Slab CH 4145 - 4135 = 10m/bay	7d/wk-1a	10d	04-May-15 08	13-May-15 18	16d			■ EB From East, Base Slab CH 4145 - 4135 = 10m/bay					
A9895	EB From East, Base Slab CH 4135 - 4125 = 10m/bay	7d/wk-1a	10d	24-May-15 08	02-Jun-15 18	6d			■ EB From East, Base Slab CH 4135 - 4125 = 10m/bay					
A9890	EB From East, Base Slab CH 4125 - 4115 = 10m/bay	7d/wk-1a	10d	09-Jun-15 08	18-Jun-15 18	0d			■ EB From East, Base Slab CH 4125 - 4115 = 10m/bay					
A9885	EB From East, Base Slab CH 4115 - 4105 = 10m/bay	7d/wk-1a	10d	19-Jun-15 08	29-Jun-15 18	0d			■ EB From East, Base Slab CH 4115 - 4105 = 10m/bay					
A9880	EB From East, Base Slab CH 4105 - 4095 = 10m/bay	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d			■ EB From East, Base Slab CH 4105 - 4095 = 10m/bay					
<b>Lining (5m/bay, 15m separation with base slab)</b>														
A9065	EB From West, Lining CH 3990 - 3995 = 1bay	7d/wk-1a	10d	03-Feb-15 08	12-Feb-15 18	4d			■ EB From West, Lining CH 3990 - 3995 = 1bay					
A9005	EB From West, Lining CH 3995 - 4000 = 1bay	7d/wk-1a	10d	13-Feb-15 08	25-Feb-15 18	4d			■ EB From West, Lining CH 3995 - 4000 = 1bay					
A9090	EB From West, Lining CH 4000 - 4005 = 1bay	7d/wk-1a	10d	26-Feb-15 08	07-Mar-15 18	4d			■ EB From West, Lining CH 4000 - 4005 = 1bay					

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

11 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2
A9050	EB From West, Lining CH 4005 - 4010 = 1bay	7d/wk-1a	10d	08-Mar-15 08	17-Mar-15 18	4d			■ EB From West, Lining CH 4005 - 4010 = 1bay				
A9055	EB From West, Lining CH 4010 - 4015 = 1bay	7d/wk-1a	10d	18-Mar-15 08	27-Mar-15 18	4d			■ EB From West, Lining CH 4010 - 4015 = 1bay				
A9080	EB From West, Lining CH 4015 - 4020 = 1bay	7d/wk-1a	10d	26-Mar-15 08	05-Apr-15 18	4d			■ EB From West, Lining CH 4015 - 4020 = 1bay				
A9070	EB From West, Lining CH 4020 - 4025 = 1bay	7d/wk-1a	10d	03-Apr-15 08	13-Apr-15 18	4d			■ EB From West, Lining CH 4020 - 4025 = 1bay				
A9075	EB From West, Lining CH 4025 - 4030 = 1bay	7d/wk-1a	10d	12-Apr-15 08	21-Apr-15 18	4d			■ EB From West, Lining CH 4025 - 4030 = 1bay				
A9080	EB From West, Lining CH 4030 - 4035 = 1bay	7d/wk-1a	10d	20-Apr-15 08	29-Apr-15 18	4d			■ EB From West, Lining CH 4030 - 4035 = 1bay				
A9085	EB From West, Lining CH 4035 - 4040 = 1bay	7d/wk-1a	10d	28-Apr-15 08	08-May-15 18	4d			■ EB From West, Lining CH 4035 - 4040 = 1bay				
A9015	EB From West, Lining CH 4040 - 4045 = 1bay	7d/wk-1a	10d	07-May-15 08	16-May-15 18	4d			■ EB From West, Lining CH 4040 - 4045 = 1bay				
A9020	EB From West, Lining CH 4045 - 4050 = 1bay	7d/wk-1a	10d	15-May-15 08	24-May-15 18	4d			■ EB From West, Lining CH 4045 - 4050 = 1bay				
A9025	EB From West, Lining CH 4050 - 4055 = 1bay	7d/wk-1a	10d	23-May-15 08	01-Jun-15 18	4d			■ EB From West, Lining CH 4050 - 4055 = 1bay				
A9030	EB From West, Lining CH 4055 - 4060 = 1bay	7d/wk-1a	10d	31-May-15 08	09-Jun-15 18	4d			■ EB From West, Lining CH 4055 - 4060 = 1bay				
A9035	EB From West, Lining CH 4060 - 4065 = 1bay	7d/wk-1a	10d	07-Jun-15 08	16-Jun-15 18	4d			■ EB From West, Lining CH 4060 - 4065 = 1bay				
A9040	EB From West, Lining CH 4065 - 4070 = 1bay	7d/wk-1a	10d	14-Jun-15 08	24-Jun-15 18	4d			■ EB From West, Lining CH 4065 - 4070 = 1bay				
A9045	EB From West, Lining CH 4070 - 4075 = 1bay	7d/wk-1a	10d	25-Jun-15 08	05-Jul-15 18	0d			■ EB From West, Lining CH 4070 - 4075 = 1bay				
A8955	EB From West, Lining CH 4075 - 4080 = 1bay	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d			■ EB From West, Lining CH 4075 - 4080 = 1bay				
A8960	EB From West, Lining CH 4080 - 4085 = 1bay	7d/wk-1a	5d	11-Jul-15 08	15-Jul-15 18	0d			■ EB From West, Lining CH 4080 - 4085 = 1bay				
A8970	EB From West, Lining CH 4085 - 4090 = 1bay	7d/wk-1a	5d	16-Jul-15 08	20-Jul-15 18	0d			■ EB From West, Lining CH 4085 - 4090 = 1bay				
A8975	EB From West, Lining CH 4090 - 4095 = 1bay	7d/wk-1a	5d	21-Jul-15 08	25-Jul-15 18	0d			■ EB From West, Lining CH 4090 - 4095 = 1bay				
A8980	EB From West, Lining CH 4095 - 4100 = 1bay	7d/wk-1a	5d	26-Jul-15 08	30-Jul-15 18	0d			■ EB From West, Lining CH 4095 - 4100 = 1bay				
A8985	EB From West, Lining CH 4100 - 4105 = 1bay	7d/wk-1a	5d	31-Jul-15 08	04-Aug-15 18	0d			■ EB From West, Lining CH 4100 - 4105 = 1bay				
A8990	EB From West, Lining CH 4105 - 4110 = 1bay	7d/wk-1a	5d	05-Aug-15 08	09-Aug-15 18	0d			■ EB From West, Lining CH 4105 - 4110 = 1bay				
A8995	EB From West, Lining CH 4110 - 4115 = 1bay	7d/wk-1a	5d	10-Aug-15 08	14-Aug-15 18	0d			■ EB From West, Lining CH 4110 - 4115 = 1bay				
A9000	EB From West, Lining CH 4115 - 4120 = 1bay	7d/wk-1a	5d	15-Aug-15 08	19-Aug-15 18	0d			■ EB From West, Lining CH 4115 - 4120 = 1bay				
A9010	EB From West, Lining CH 4120 - 4125 = 1bay	7d/wk-1a	5d	20-Aug-15 08	24-Aug-15 18	0d			■ EB From West, Lining CH 4120 - 4125 = 1bay				
A8965	EB From West, Lining CH 4125 - 4130 = 1bay	7d/wk-1a	5d	25-Aug-15 08	29-Aug-15 18	0d			■ EB From West, Lining CH 4125 - 4130 = 1bay				
A8935	EB From West, Lining CH 4130 - 4135 = 1bay	7d/wk-1a	5d	30-Aug-15 08	03-Sep-15 18	0d			■ EB From West, Lining CH 4130 - 4135 = 1bay				
A8940	EB From West, Lining CH 4135 - 4140 = 1bay	7d/wk-1a	5d	04-Sep-15 08	08-Sep-15 18	0d			■ EB From West, Lining CH 4135 - 4140 = 1bay				
A8945	EB From West, Lining CH 4140 - 4145 = 1bay	7d/wk-1a	5d	09-Sep-15 08	13-Sep-15 18	0d			■ EB From West, Lining CH 4140 - 4145 = 1bay				
A8950	EB From West, Lining CH 4145 - 4149.5 = 4.5m	7d/wk-1a	5d	14-Sep-15 08	18-Sep-15 18	0d			■ EB From West, Lining CH 4145 - 4149.5 = 4.5m				

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

12 of 18

**China State Construction Engineering (Hong Kong) Ltd**

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

**WORKS PROGRAMME REV. M**

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep-...	1st submission		



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016					
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3		
OHVD(10m/bay) / Utility Trough																
A9095	EB From West OHVD and utility trough =, 167= 17 bays @ 10m/bay @ 7d/bay	7d/wk-1a	120d	03-Jul-15 08	02-Nov-15 18	0d										
WB Outer Tunnel Excavation																
From West (TPCWAE)																
Outer Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																
A9651	WB, Outer Heading From West, CH 4085- 4092.5 = 7.5m @ 2d/m	7d/wk-1a	15d	13-Sep-14 08 A	30-Sep-14 18	163d										
Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)																
A9680	WB, Outer Bench From West, CH 4025- 4035 = 10m	7d/wk-1a	15d	12-Oct-14 08	26-Oct-14 18	163d										
A9665	WB, Outer Bench From West, CH 4035- 4045 = 10m	7d/wk-1a	15d	27-Oct-14 08	10-Nov-14 18	163d										
A9670	WB, Outer Bench From West, CH 4045- 4055 = 10m	7d/wk-1a	15d	11-Nov-14 08	25-Nov-14 18	163d										
A9675	WB, Outer Bench From West, CH 4055- 4065 = 10m	7d/wk-1a	15d	26-Nov-14 08	10-Dec-14 18	163d										
A9700	WB, Outer Bench From West, CH 4065- 4075 = 10m	7d/wk-1a	15d	11-Dec-14 08	26-Dec-14 18	163d										
A9701	WB, Outer Bench From West, CH 4075- 4082.5 = 7.5m	7d/wk-1a	15d	27-Dec-14 08	11-Jan-15 18	163d										
From East (TS4)																
Outer Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																
A9730	WB, Outer Heading From East, CH 4105- 4092.5 = 12.5m @2d/m	7d/wk-1a	25d	30-Aug-14 08 A	30-Sep-14 18	168d										
Outer Bench Excavation (1.5d-2d/m, 20m separation with heading)																
A9740	WB, Outer Bench From East, CH 4136- 4135 = 1m	7d/wk-1a	2d	12-Oct-14 08	13-Oct-14 18	168d										
A9770	WB, Outer Bench From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	14-Oct-14 08	28-Oct-14 18	168d										
A9745	WB, Outer Bench From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	28-Oct-14 08	11-Nov-14 18	168d										
A9750	WB, Outer Bench From East, CH 4115- 4105 = 10m	7d/wk-1a	15d	11-Nov-14 08	25-Nov-14 18	168d										
A9755	WB, Outer Bench From East, CH 4105- 4095 = 10m	7d/wk-1a	15d	26-Nov-14 08	10-Dec-14 18	168d										
A9760	WB, Outer Bench From East, CH 4095- 4082.5 = 12.5m	7d/wk-1a	25d	11-Dec-14 08	06-Jan-15 18	168d										
WB (Inner Tunnel Excavation + Lining)																
From West (TPCWAE)																
Inner Heading Excavation (2-3d/m, 24h/day work shift, 7d/week, no work on statutory holiday)																
A9130	WB, Inner Heading From West, CH 3993- 4005 = 12m @3d/m	7d/wk-1a	50d	29-Sep-14 08	18-Nov-14 18	0d										
A9135	WB, Inner Heading From West, CH 4005- 4015 = 10m @2d/m	7d/wk-1a	20d	19-Nov-14 08	08-Dec-14 18	0d										
A9140	WB, Inner Heading From West, CH 4015- 4025 = 10m @2d/m	7d/wk-1a	20d	09-Dec-14 08	29-Dec-14 18	0d										

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

13 of 18

**China State Construction Engineering (Hong Kong) Ltd**

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

**WORKS PROGRAMME REV. M**

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep...	1st submission		



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
A9100	WB,Inner Heading From West, CH 4025- 4035 = 10m @2d/m	7d/wk-1a	20d	30-Dec-14 08	19-Jan-15 18	0d		■	WB,Inner Heading From West, CH 4025- 4035 = 10m @2d/m					
A9105	WB,Inner Heading From West, CH 4035- 4045 = 10m @2d/m	7d/wk-1a	20d	20-Jan-15 08	08-Feb-15 18	0d		■	WB,Inner Heading From West, CH 4035- 4045 = 10m @2d/m					
A9110	WB,Inner Heading From West, CH 4045- 4055 = 10m @2d/m	7d/wk-1a	20d	09-Feb-15 08	03-Mar-15 18	0d		■	WB,Inner Heading From West, CH 4045- 4055 = 10m @2d/m					
A9115	WB,Inner Heading From West, CH 4055- 4065 = 10m @ 2d/m	7d/wk-1a	20d	04-Mar-15 08	23-Mar-15 18	0d		■	WB,Inner Heading From West, CH 4055- 4065 = 10m @ 2d/m					
A9120	WB,Inner Heading From West, CH 4065- 4075 = 10m, @ 2d/m	7d/wk-1a	20d	24-Mar-15 08	13-Apr-15 18	0d		■	WB,Inner Heading From West, CH 4065- 4075 = 10m, @ 2d/m					
A9125	WB,Inner Heading From West, CH 4075- 4085 = 10m @ 2d/m	7d/wk-1a	20d	14-Apr-15 08	04-May-15 18	0d		■	WB,Inner Heading From West, CH 4075- 4085 = 10m @ 2d/m					
<b>Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)</b>														
A9180	WB,Inner Bench From West, CH 3993- 4005 = 12m	7d/wk-1a	18d	30-Dec-14 08	17-Jan-15 18	27d		■	WB,Inner Bench From West, CH 3993- 4005 = 12m					
A9205	WB,Inner Bench From West, CH 4005- 4015 = 10m	7d/wk-1a	15d	20-Jan-15 08	03-Feb-15 18	25d		■	WB,Inner Bench From West, CH 4005- 4015 = 10m					
A9190	WB,Inner Bench From West, CH 4015- 4025 = 10m	7d/wk-1a	15d	09-Feb-15 08	26-Feb-15 18	20d		■	WB,Inner Bench From West, CH 4015- 4025 = 10m					
A9185	WB,Inner Bench From West, CH 4025- 4035 = 10m	7d/wk-1a	15d	04-Mar-15 08	18-Mar-15 18	15d		■	WB,Inner Bench From West, CH 4025- 4035 = 10m					
A9155	WB,Inner Bench From West, CH 4035- 4045 = 10m	7d/wk-1a	15d	24-Mar-15 08	08-Apr-15 18	10d		■	WB,Inner Bench From West, CH 4035- 4045 = 10m					
A9160	WB,Inner Bench From West, CH 4045- 4055 = 10m	7d/wk-1a	15d	14-Apr-15 08	28-Apr-15 18	5d		■	WB,Inner Bench From West, CH 4045- 4055 = 10m					
A9165	WB,Inner Bench From West, CH 4055- 4065 = 10m	7d/wk-1a	15d	05-May-15 08	19-May-15 18	0d		■	WB,Inner Bench From West, CH 4055- 4065 = 10m					
A9170	WB,Inner Bench From West, CH 4065- 4075 = 10m	7d/wk-1a	15d	20-May-15 08	03-Jun-15 18	0d		■	WB,Inner Bench From West, CH 4065- 4075 = 10m					
A9175	WB,Inner Bench From West, CH 4075- 4085 = 10m	7d/wk-1a	15d	04-Jun-15 08	18-Jun-15 18	0d		■	WB,Inner Bench From West, CH 4075- 4085 = 10m					
<b>From East (TS4)</b>														
<b>Inner Heading Excavation (2d/m, 24h/day work shift, 7d/week, no work on statutory holiday)</b>														
A9210	WB,Inner Heading From East, CH 4135- 4125 = 10m @2d/m	7d/wk-1a	20d	14-Jan-15 08	02-Feb-15 18	6d		■	WB,Inner Heading From East, CH 4135- 4125 = 10m @2d/m					
A9215	WB,Inner Heading From East, CH 4125- 4115 = 10m @2d/m	7d/wk-1a	20d	03-Feb-15 08	25-Feb-15 18	6d		■	WB,Inner Heading From East, CH 4125- 4115 = 10m @2d/m					
A9230	WB,Inner Heading From East, CH 4115- 4105 = 10m @2d/m	7d/wk-1a	20d	26-Feb-15 08	17-Mar-15 18	6d		■	WB,Inner Heading From East, CH 4115- 4105 = 10m @2d/m					
A9232	WB,Inner Heading From East, CH 4105- 4095 = 10m @2d/m	7d/wk-1a	20d	18-Mar-15 08	07-Apr-15 18	6d		■	WB,Inner Heading From East, CH 4105- 4095 = 10m @2d/m					
A9225	WB,Inner Heading From East, CH 4095- 4085 = 10m @2d/m	7d/wk-1a	20d	08-Apr-15 08	27-Apr-15 18	6d		■	WB,Inner Heading From East, CH 4095- 4085 = 10m @2d/m					
<b>Inner Bench Excavation (1.5d-2d/m, 20m separation with heading)</b>														
A9235	WB,Inner Bench From East, CH 4135- 4125 = 10m	7d/wk-1a	15d	18-Mar-15 08	01-Apr-15 18	16d		■	WB,Inner Bench From East, CH 4135- 4125 = 10m					
A9240	WB,Inner Bench From East, CH 4125- 4115 = 10m	7d/wk-1a	15d	08-Apr-15 08	22-Apr-15 18	11d		■	WB,Inner Bench From East, CH 4125- 4115 = 10m					
A9245	WB,Inner Bench From East, CH 4115- 4105 = 10m	7d/wk-1a	15d	28-Apr-15 08	13-May-15 18	6d		■	WB,Inner Bench From East, CH 4115- 4105 = 10m					
A9247	WB,Inner Bench From East, CH 4105- 4095 = 10m	7d/wk-1a	15d	14-May-15 08	28-May-15 18	6d		■	WB,Inner Bench From East, CH 4105- 4095 = 10m					
A9250	WB,Inner Bench From East, CH 4095- 4085 = 10m	7d/wk-1a	15d	29-May-15 08	12-Jun-15 18	6d		■	WB,Inner Bench From East, CH 4095- 4085 = 10m					

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

14 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016						
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3			
<b>Tunnel Lining Works</b>																	
<b>From West Base Slab (10m/bay, 10m separation with benching excavation)</b>																	
A9295	WB From West, Base Slab CH 3990 - 3995 = 5m bay	7d/wk-1a	10d	18-Jan-15 08	27-Jan-15 18	37d											
A9320	WB From West, Base Slab CH 3995 - 4005 = 10m/bay	7d/wk-1a	10d	04-Feb-15 08	13-Feb-15 18	30d											
A9255	WB From West, Base Slab CH 4005 - 4015 = 10m/bay	7d/wk-1a	10d	27-Feb-15 08	08-Mar-15 18	50d											
A9280	WB From West, Base Slab CH 4015 - 4025 = 10m/bay	7d/wk-1a	10d	19-Mar-15 08	28-Mar-15 18	40d											
A9265	WB From West, Base Slab CH 4025 - 4035 = 10m/bay	7d/wk-1a	10d	09-Apr-15 08	18-Apr-15 18	30d											
A9300	WB From West, Base Slab CH 4035 - 4045 = 10m/bay	7d/wk-1a	10d	29-Apr-15 08	09-May-15 18	20d											
A9325	WB From West, Base Slab CH 4045 - 4055 = 10m/bay	7d/wk-1a	10d	20-May-15 08	29-May-15 18	10d											
A9305	WB From West, Base Slab CH 4055 - 4065 = 10m/bay	7d/wk-1a	10d	04-Jun-15 08	13-Jun-15 18	5d											
A9310	WB From West, Base Slab CH 4065 - 4075 = 10m/bay	7d/wk-1a	10d	19-Jun-15 08	29-Jun-15 18	0d											
A9315	WB From West, Base Slab CH 4075 - 4080 = 5m	7d/wk-1a	10d	30-Jun-15 08	10-Jul-15 18	0d											
<b>From East Base Slab (10m/bay, 10m separation with benching excavation)</b>																	
A9960	WB From East, Base Slab CH 4135 - 4125 = 10m/bay	7d/wk-1a	10d	23-Apr-15 08	03-May-15 18	26d											
A9955	WB From East, Base Slab CH 4125 - 4115 = 10m/bay	7d/wk-1a	10d	14-May-15 08	23-May-15 18	16d											
A9950	WB From East, Base Slab CH 4115 - 4105 = 10m/bay	7d/wk-1a	10d	29-May-15 08	07-Jun-15 18	11d											
A9945	WB From East, Base Slab CH 4105 - 4095 = 10m/bay	7d/wk-1a	10d	13-Jun-15 08	23-Jun-15 18	6d											
A9940	WB From East, Base Slab CH 4095 - 4085 = 10m/bay	7d/wk-1a	10d	24-Jun-15 08	04-Jul-15 18	6d											
A9941	WB From East, Base Slab CH 4085 - 4080 = 5m	7d/wk-1a	10d	05-Jul-15 08	14-Jul-15 18	6d											
<b>Lining (5m/bay, 10m separation with base slab)</b>																	
A9430	WB From West, Lining CH 3990 - 3995 = 1bay	7d/wk-1a	7d	14-Feb-15 08	23-Feb-15 18	30d											
A9470	WB From West, Lining CH 3995 - 4000 = 1bay	7d/wk-1a	7d	24-Feb-15 08	02-Mar-15 18	30d											
A9435	WB From West, Lining CH 4000 - 4005 = 1bay	7d/wk-1a	7d	03-Mar-15 08	09-Mar-15 18	30d											
A9360	WB From West, Lining CH 4005 - 4010 = 1bay	7d/wk-1a	7d	10-Mar-15 08	16-Mar-15 18	30d											
A9365	WB From West, Lining CH 4010 - 4015 = 1bay	7d/wk-1a	7d	17-Mar-15 08	23-Mar-15 18	30d											
A9370	WB From West, Lining CH 4015 - 4020 = 1bay	7d/wk-1a	7d	24-Mar-15 08	30-Mar-15 18	30d											
A9375	WB From West, Lining CH 4020 - 4025 = 1bay	7d/wk-1a	7d	31-Mar-15 08	07-Apr-15 18	30d											
A9380	WB From West, Lining CH 4025 - 4030 = 1bay	7d/wk-1a	7d	08-Apr-15 08	14-Apr-15 18	30d											
A9385	WB From West, Lining CH 4030 - 4035 = 1bay	7d/wk-1a	7d	15-Apr-15 08	21-Apr-15 18	30d											

- Summary Bar
- ▬ Actual Level of Effort
- ▬ Actual Work
- ▬ Remaining Work
- ▬ Critical Remaining Work
- ◆ Milestone

15 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

WORKS PROGRAMME REV. M

Prepared by William Kaluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



中國建築工程(香港)有限公司  
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016		
							Q4	Q1	Q2	Q3	Q4	Q1	Q2
A9390	WB From West, Lining CH 4035 - 4040 = 1bay	7d/wk-1a	7d	22-Apr-15 08	28-Apr-15 18	30d			■ WB From West, Lining CH 4035 - 4040 = 1bay				
A9330	WB From West, Lining CH 4040 - 4045 = 1bay	7d/wk-1a	7d	29-Apr-15 08	06-May-15 18	30d			■ WB From West, Lining CH 4040 - 4045 = 1bay				
A9335	WB From West, Lining CH 4045 - 4050 = 1bay	7d/wk-1a	7d	07-May-15 08	13-May-15 18	30d			■ WB From West, Lining CH 4045 - 4050 = 1bay				
A9340	WB From West, Lining CH 4050 - 4055 = 1bay	7d/wk-1a	7d	14-May-15 08	20-May-15 18	30d			■ WB From West, Lining CH 4050 - 4055 = 1bay				
A9345	WB From West, Lining CH 4055 - 4060 = 1bay	7d/wk-1a	7d	21-May-15 08	27-May-15 18	30d			■ WB From West, Lining CH 4055 - 4060 = 1bay				
A9350	WB From West, Lining CH 4060 - 4065 = 1bay	7d/wk-1a	7d	28-May-15 08	03-Jun-15 18	30d			■ WB From West, Lining CH 4060 - 4065 = 1bay				
A9355	WB From West, Lining CH 4065 - 4070 = 1bay	7d/wk-1a	5d	04-Jun-15 08	08-Jun-15 18	30d			■ WB From West, Lining CH 4065 - 4070 = 1bay				
A9415	WB From West, Lining CH 4070 - 4075 = 1bay	7d/wk-1a	5d	11-Jul-15 08	15-Jul-15 18	0d			■ WB From West, Lining CH 4070 - 4075 = 1bay				
A9475	WB From West, Lining CH 4075 - 4080 = 1bay	7d/wk-1a	5d	16-Jul-15 08	20-Jul-15 18	0d			■ WB From West, Lining CH 4075 - 4080 = 1bay				
A9440	WB From West, Lining CH 4080 - 4085 = 1bay	7d/wk-1a	5d	21-Jul-15 08	25-Jul-15 18	0d			■ WB From West, Lining CH 4080 - 4085 = 1bay				
A9445	WB From West, Lining CH 4085 - 4090 = 1bay	7d/wk-1a	5d	26-Jul-15 08	30-Jul-15 18	0d			■ WB From West, Lining CH 4085 - 4090 = 1bay				
A9450	WB From West, Lining CH 4090 - 4095 = 1bay	7d/wk-1a	5d	31-Jul-15 08	04-Aug-15 18	0d			■ WB From West, Lining CH 4090 - 4095 = 1bay				
A9455	WB From West, Lining CH 4095 - 4100 = 1bay	7d/wk-1a	5d	05-Aug-15 08	09-Aug-15 18	0d			■ WB From West, Lining CH 4095 - 4100 = 1bay				
A9420	WB From West, Lining CH 4100 - 4105 = 1bay	7d/wk-1a	5d	10-Aug-15 08	14-Aug-15 18	0d			■ WB From West, Lining CH 4100 - 4105 = 1bay				
A9425	WB From West, Lining CH 4105 - 4110 = 1bay	7d/wk-1a	5d	15-Aug-15 08	19-Aug-15 18	0d			■ WB From West, Lining CH 4105 - 4110 = 1bay				
A9460	WB From West, Lining CH 4110 - 4115 = 1bay	7d/wk-1a	5d	20-Aug-15 08	24-Aug-15 18	0d			■ WB From West, Lining CH 4110 - 4115 = 1bay				
A9465	WB From West, Lining CH 4115 - 4120 = 1bay	7d/wk-1a	5d	25-Aug-15 08	29-Aug-15 18	0d			■ WB From West, Lining CH 4115 - 4120 = 1bay				
A9395	WB From West, Lining CH 4120 - 4125 = 1bay	7d/wk-1a	5d	30-Aug-15 08	03-Sep-15 18	0d			■ WB From West, Lining CH 4120 - 4125 = 1bay				
A9400	WB From West, Lining CH 4125 - 4130 = 1bay	7d/wk-1a	5d	04-Sep-15 08	08-Sep-15 18	0d			■ WB From West, Lining CH 4125 - 4130 = 1bay				
A9405	WB From West, Lining CH 4130 - 4135 = 1bay	7d/wk-1a	5d	09-Sep-15 08	13-Sep-15 18	0d			■ WB From West, Lining CH 4130 - 4135 = 1bay				
A9410	WB From West, Lining CH 4135 - 4136.5 = 1bay	7d/wk-1a	5d	14-Sep-15 08	18-Sep-15 18	0d			■ WB From West, Lining CH 4135 - 4136.5 = 1bay				
OHVD(10m/bay) / Utility Trough													
A9480	WB From West OHVD and utility trough =, 153= 16 bays @ 10m/bay @ 7d/bay	7d/wk-1a	115d	08-Jul-15 08	02-Nov-15 18	0d			■ WB From West OHVD and utility trough =, 153= 16 bays @ 10				
Completion of KD10- Section 5													
A8445	KD10- Section 2: Completion of Mined Tunnel Works (orig. Target KD10- 2 Nov 2015)	7d/wk-2	0d		02-Nov-15 18*	0d							◆ KD10- Section 2: Completion of Mined Tunnel Works (orig. Tar
Interface works with other Contracts													
S5_60115	Handover TZ6 to MTR	7d/wk-2	0d		30-Sep-14 18	-249d			◆ Handover TZ6 to MTR				
S6_5283	Handover TZ4 to CWB(T2)	7d/wk-2	0d		10-Nov-14 18	-290d			◆ Handover TZ4 to CWB(T2)				
S6_5275	Provide access to CWB (CC) Contractor- TS1 & TS2	7d/wk-2	0d		21-Nov-14 18*	-85d			◆ Provide access to CWB (CC) Contractor- TS1 & TS2				

Summary Bar  
 Actual Level of Effort  
 Actual Work  
 Remaining Work  
 Critical Remaining Work  
 Milestone

16 of 18

**China State Construction Engineering (Hong Kong) Ltd**  
 Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)  
**WORKS PROGRAMME REV. M**

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep...	1st submission		



Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
SB_5280	Provide access to CWB (CC) Contractor- TS4, TPCWA, Mined Tunnel	7d/wk-2	0d		31-Mar-16 18*	-124d								◆ Provide access to CWB (CC) C
<b>Stage and Section Completion</b>														
KD_5735	KD8 - Completion of Section 3, (1326d)	7d/wk-2	0d		30-Sep-14 18*	-86d	◆ KD8 - Completion of Section 3, (1326d)							
KD_5720	KD5 - Achievement of Stage 5, (1152d)	7d/wk-2	0d		16-Oct-14 18*	-323d	◆ KD5 - Achievement of Stage 5, (1152d)							
KD_5760	KD13 - Completion of Section 7B, (1152d)	7d/wk-2	0d		17-Nov-14 18*	-353d	◆ KD13 - Completion of Section 7B, (1152d)							
KD_5730	KD7 - Completion of Section 2, (1152d)	7d/wk-2	0d		17-Nov-14 18*	-297d	◆ KD7 - Completion of Section 2, (1152d)							
KD_5740	KD9 - Completion of Section 4, (1739d)	7d/wk-2	0d		10-Nov-15 18*	-132d							◆ KD9 - Completion of Section 4, (1739d)	
KD_5745	KD10 - Completion of Section 5, (1863d)	7d/wk-2	0d		25-Mar-16 18	-144d							◆ KD10 - Completion of Section 5, (	
KD_5750	KD11 - Completion of Section 6, (1949d)	7d/wk-2	0d		23-May-16 18*	-121d							◆ KD11 - Completion of	
<b>Portion Handover Date</b>														
CD_5685	Portion Handover - Portion IV(4), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion IV(4), KD8 +28							
CD_5680	Portion Handover - Portion V (5), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion V (5), KD8 +28							
CD_5695	Portion Handover - Portion VI (6), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion VI (6), KD8 +28							
CD_5735	Portion Handover - Portion XIII (13B), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion XIII (13B), KD8 +28							
CD_5790	Portion Handover - Portion XXII (22), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion XXII (22), KD8 +28							
CD_5670	Portion Handover - Portion III (3), KD8 +28	7d/wk-2	0d		28-Oct-14 18*	-50d	◆ Portion Handover - Portion III (3), KD8 +28							
CD_5720	Portion Handover - Portion XIII (13A), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XIII (13A), KD7 +28							
CD_5705	Portion Handover - Portion VIII (8), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion VIII (8), KD7 +28							
CD_5730	Portion Handover - Portion XIV (14A), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XIV (14A), KD7 +28							
CD_5740	Portion Handover - Portion XV (15), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XV (15), KD7 +28							
CD_5805	Portion Handover - Portion XXIII (23), KD7 +28	7d/wk-2	0d		15-Dec-14 18*	-79d	◆ Portion Handover - Portion XXIII (23), KD7 +28							
CD_5775	Portion Handover - Portion XVIII (18), KD10 +28	7d/wk-2	0d		30-Nov-15 18*	0d							◆ Portion Handover - Portion XVIII (18), KD10 +28	
CD_5710	Portion Handover - Portion XI (11), KD9 +28	7d/wk-2	0d		27-Dec-15 18*	0d							◆ Portion Handover - Portion XI (11), KD9 +28	
CD_5700	Portion Handover - Portion IX (9), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d							◆ Portion Handover - Portion	
CD_5745	Portion Handover - Portion XIV (14B), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d							◆ Portion Handover - Portion	
CD_5755	Portion Handover - Portion XVI (16), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d							◆ Portion Handover - Portion	
CD_5750	Portion Handover - Portion XVII (17), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d							◆ Portion Handover - Portion	
CD_5760	Portion Handover - Portion XIX (19), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d							◆ Portion Handover - Portion	
CD_5780	Portion Handover - Portion XX (20B), KD10 +28	7d/wk-2	0d		22-Apr-16 18*	-52d							◆ Portion Handover - Portion	

- █ Summary Bar
- ▬ Actual Level of Effort
- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone

17 of 18

China State Construction Engineering (Hong Kong) Ltd

Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)

**WORKS PROGRAMME REV. M**

Prepared by William Caluza

Date	Revision	Checked	Approved
26-Sep...	1st submission		



**中國建築工程(香港)有限公司**  
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Calendar	Original Duration	Start	Finish	Total Float	2015				2016			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
CD_5690	Portion Handover - Portion VII (7), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5725	Portion Handover - Portion XII (12), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5715	Portion Handover - Portion X (10), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5785	Portion Handover - Portion XXA (20A), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov
CD_5795	Portion Handover - Portion XXI (21), KD11 +28	7d/wk-2	0d		20-Jun-16 18	0d								◆ Portion Handov

- Summary Bar
- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ ◆ Milestone

18 of 18

China State Construction Engineering (Hong Kong) Ltd  
 Contract No. HY/2009/15 - Central Wan Chai By Pass - Tunnel ( Causeway Bay Typhoon Shelter Section)  
**WORKS PROGRAMME REV. M**

Prepared by William Caluza			
Date	Revision	Checked	Approved
26-Sep...	1st submission		



**中國建築工程(香港)有限公司**  
 CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Activity ID	Activity Name	Orig Dur	Scheduled/Actual Start	Scheduled/Actual Finish	Total Float	Calendar	2015					
							Aug	Sep	Oct	Nov	Dec	
<b>Three Months Rolling Programme 2015-08-20 (dd 20-Aug-15)</b>												
<b>Programme Milestones (Revised up to EOTO No.12 Issued on 15-Jun-15)</b>												
<b>Contractual Completion Dates</b>												
KDC0170	Section 9B Works (2105 days) - CWB Structure (CH3400 Eastward) (3-Nov-15)	0		03-Nov-15*	0	Calendar Day						
<b>Soft Landscaping &amp; Establishment Key Dates</b>												
KDC0150	Section 8D Works (1838 days) - Establishment Works in Area 8 (10-Feb-15)	0		20-Aug-15*	-192	Calendar Day						
<b>Possession of Site</b>												
PS0070	Possession of Portion 7 - Eastern Bulkhead	0	16-Sep-15*		-60	Calendar Day						
<b>Preliminaries</b>												
<b>Interface with Others</b>												
PRE0950	Permanent Diversion of Box Culvert M by HK2009/01	0		30-Aug-15*	-469	Calendar Day						
<b>Critical Submission &amp; Approval</b>												
PRE-SUB-1000B	Temp Covered Walkway Capping Beam - Design Approval by AECOM	30	19-Jun-13 A	18-Sep-15	348	Calendar Day						
PRE-SUB-1010B	Temp Covered Walkway Cover System (PS30.5) - Design Approval by AECOM	30	12-Jun-14 A	15-Sep-15	348	Calendar Day						
<b>CSD for CWB Tunnel</b>												
PRE-CSD-2030B	Tunnel Portion 2 - Redesigned CWB Tunnel Structure Design Submission Approval by AECOM & GEO	60	16-Nov-13 A	28-Aug-15	67	Calendar Day						
PRE-CSD-3000B	Tunnel Portion 3&4 - Redesigned Temp D-Wall Submission Approval by AECOM & GEO	30	08-Jun-13 A	11-Sep-15	53	Calendar Day						
PRE-CSD-3010B	Tunnel Portion 3&4 - ELS Submission Approval by AECOM & GEO	60	17-Jan-14 A	18-Sep-15	-316	Calendar Day						
PRE-CSD-5000B	Tunnel Portion 5 - Temp D-Wall Submission Approval by AECOM & GEO	60	15-Aug-13 A	21-Sep-15	-389	Calendar Day						
PRE-CSD-5010B	Tunnel Portion 5 - ELS Submission Approval by AECOM & GEO	60	09-Apr-15 A	17-Oct-15	-363	Calendar Day						
<b>Section 3 of the Works - Re-provisioning of Government Helipad and Public Toilet</b>												
<b>Outstanding Works</b>												
S3-0070-1489	Reinstatement of armour rock, retaining walls & now covered walkway along Expo Drive East	254	11-Aug-12 A	01-May-16*	-287	Calendar Day						
<b>Section 9B of the Works - CWB Tunnel Structure (CH3400 - CH3796)</b>												
<b>Tunnel Portion 1 (CH3500-CH3630)</b>												
<b>CWB Structural Works</b>												
S9B-T1-4600	Remove Inclined Struts and King Posts (Bay 1 to Bay 6)	45	29-Jun-15 A	31-Aug-15	-43	HK Working Day						
S9B-T1-5106	Construct Roadside Barriers (Bay 1 to Bay 6)	30	19-Nov-15	23-Dec-15	-43	HK Working Day						
<b>Tunnel Portion 2 (CH3425-CH3500)</b>												
<b>CWB Structural Works</b>												
S9B-T2-5100	Construct Roadside Barriers (Bay 1 to Bay 6)	65	01-Sep-15	18-Nov-15	-43	HK Working Day						
<b>Bay 1</b>												
S9B-T2-B1-3260	Roof - Waterproofing	4	01-Sep-15*	04-Sep-15	-23	HK Working Day						
S9B-T2-B1-3270	Roof - Scaffolding Dismantling	3	20-Aug-15	22-Aug-15	14	HK Working Day						
<b>Bay 2</b>												
S9B-T2-B2-3210	Roof - Waterproofing	4	05-Sep-15	09-Sep-15	93	HK Working Day						
S9B-T2-B2-3220	Roof - Scaffolding Dismantling	3	20-Aug-15	22-Aug-15	14	HK Working Day						
<b>Bay 3</b>												
S9B-T2-B3-3210	Roof - Waterproofing	4	10-Sep-15	14-Sep-15	93	HK Working Day						
S9B-T2-B3-3220	Roof - Scaffolding Dismantling	3	20-Aug-15	22-Aug-15	14	HK Working Day						
<b>Bay 4</b>												
S9B-T2-B4-3180	Roof - Formwork	9	19-Jul-15 A	26-Aug-15	-14	HK Working Day						
S9B-T2-B4-3190	Roof - Rebar Fixing	10	27-Aug-15	07-Sep-15	-14	HK Working Day						
S9B-T2-B4-3200	Roof - Concrete & Curing	14	08-Sep-15	21-Sep-15	-17	Calendar Day						
S9B-T2-B4-3210	Roof - Waterproofing	4	22-Sep-15	25-Sep-15	83	HK Working Day						
S9B-T2-B4-3220	Roof - Scaffolding Dismantling	3	22-Sep-15	24-Sep-15	-14	HK Working Day						
<b>Bay 5</b>												
S9B-T2-B5-3110	OHVD Base Slab - Scaffolding Erection	4	19-Aug-15 A	21-Aug-15	-46	HK Working Day						
S9B-T2-B5-3120	OHVD Base Slab - Waterproofing to Upper Side Wall	3	20-Aug-15	22-Aug-15	-46	HK Working Day						
S9B-T2-B5-3130	OHVD Base Slab - Formwork	3	24-Aug-15	26-Aug-15	-46	HK Working Day						
S9B-T2-B5-3140	OHVD Base Slab - Rebar Fixing	4	27-Aug-15	31-Aug-15	-46	HK Working Day						
S9B-T2-B5-3150	OHVD Base Slab - Concrete, Curing & Formwork Dismantling	14	01-Sep-15	14-Sep-15	-54	Calendar Day						
S9B-T2-B5-3160	OHVD Hanger Wall - Formwork, Rebar & Concrete	3	04-Sep-15	07-Sep-15	-40	HK Working Day						
S9B-T2-B5-3170	Roof - Scaffolding Erection for Roof	7	15-Sep-15	22-Sep-15	-46	HK Working Day						

- ◆ Milestones
- ◆ Critical Milestones
- █ Current Works
- █ Critical Works

**CHUN WO - CRGL  
JOINT VENTURE**

**CEDD CONTRACT NO. HK/2009/02  
WD II - Central Wanchai Bypass at Wan Chai East (Contract 2)  
3-MONTH ROLLING PROGRAMME (dd 20-Aug-15)**

Date	Revision	Checked	Approved
20-Aug-15	3MRP		





Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Schedule																											
					June 2015	July 2015	August 2015	September 2015	October 2015	November 2015	December 2015	January 2016	February 2016	March 2016	April 2016	May 2016	June 2016	July 2016	August 2016	September 2016												
<b>HK/2012/08 Revised Works Programme Rev.4_1(Final)</b>																																
<b>Dredging and Reclamation</b>																																
<b>Marine Work Construction</b>																																
<b>Zone CRIII</b>																																
<b>Dredging - Zone CRIII</b>																																
<b>CRIII - Temporary Pipe Pile Wave Wall (1st Stage)</b>																																
MAR12360	CRIII - temp pipe pile wall (34-197) - install 610 dia. pipe pile [Remaining 28 nos. @750c/c]	42	18-Oct-14 A	18-Aug-15	[Gantt bar from 18-Oct-14 to 18-Aug-15]																											
<b>CRIII - Temporary Pipe Pile Wave Wall (2nd Stage)</b>																																
MAR10035	CRIII - temp pipe pile wall (1-33) - relocate interim landing steps	0		06-Jul-15*	[Gantt bar from 06-Jul-15 to 06-Jul-15]																											
MAR10040	CRIII - temp pipe pile wall (1-33) - install 610 dia. pipe pile [33nos. @750c/c]	40	07-Jul-15	21-Aug-15	[Gantt bar from 07-Jul-15 to 21-Aug-15]																											
<b>Dredging at Zone CRIII</b>																																
<b>2nd Stage of Work (Types 1B(4) &amp; 2D)</b>																																
MAR16095	Zone CRIII - 2nd stage - Remove existing rock armour [B5-E5] after relocating interim landing steps	10	30-Aug-15	08-Sep-15	[Gantt bar from 30-Aug-15 to 08-Sep-15]																											
<b>Zone A2</b>																																
<b>Seawall Construction - Zone A2</b>																																
MAR10775	Zone A2 - seawall - Type 4, 13 - lay toe block and leveling stone in line with backfilling in zone A2(2)	18	30-Jun-15	17-Jul-15	[Gantt bar from 30-Jun-15 to 17-Jul-15]																											
MAR10780	Zone A2 - seawall - install block seawall Type 4 to -1.5mPD	14	18-Jul-15	31-Jul-15	[Gantt bar from 18-Jul-15 to 31-Jul-15]																											
MAR10800	Zone A2 - seawall - install block seawall Type 13 to -1.5mPD	14	18-Jul-15	31-Jul-15	[Gantt bar from 18-Jul-15 to 31-Jul-15]																											
MAR10805	Zone A2 - seawall - install block seawall Type 4 from -1.5 to +4.0mPD	10	01-Aug-15	12-Aug-15	[Gantt bar from 01-Aug-15 to 12-Aug-15]																											
MAR10807	Zone A2 - seawall - install block seawall Type 13 from -1.5 to +4.0mPD	10	01-Aug-15	12-Aug-15	[Gantt bar from 01-Aug-15 to 12-Aug-15]																											
MAR10815	Zone A2 - seawall - place type A behind seawall Type 4 and Type 13 up to -1.5 mPD	7	13-Aug-15	20-Aug-15	[Gantt bar from 13-Aug-15 to 20-Aug-15]																											
MAR10817	Zone A2 - seawall - lay geotextile and filter behind seawall Type 4 and Type 13 up to -1.5 mPD	7	21-Aug-15	28-Aug-15	[Gantt bar from 21-Aug-15 to 28-Aug-15]																											
<b>Filling - Zone A2</b>																																
MAR20365	Zone A2(2) - Public Fill -4.0 to +4.0mPD (behind Type 4 & 13 for temp channel outlet)	28	01-Aug-15	28-Aug-15	[Gantt bar from 01-Aug-15 to 28-Aug-15]																											
<b>Zone C</b>																																
<b>Dredging - Zone C</b>																																
MAR11520	Zone C - Cut existing pipe pile (2 nos.)	30	28-Jul-15	31-Aug-15	[Gantt bar from 28-Jul-15 to 31-Aug-15]																											
<b>Zone D</b>																																
<b>Seawall Construction - Zone D</b>																																
<b>Seawall 2C-L</b>																																
MAR12264	Zone D - Pipe Pile & demolish existing seawall	35	01-Feb-15 A	10-Aug-15	[Gantt bar from 01-Feb-15 to 10-Aug-15]																											
MAR12265	Zone D - complete fabrication of Caisson Seawall 2C-L and ready for delivery	0		30-Jul-15*	[Gantt bar from 30-Jul-15 to 30-Jul-15]																											
MAR12270	Zone D - fill rock mound for Seawall 2C-L	6	11-Aug-15	16-Aug-15	[Gantt bar from 11-Aug-15 to 16-Aug-15]																											
MAR12275	Zone D - lay toe block and level stone for Seawall 2C-L	8	17-Aug-15	25-Aug-15	[Gantt bar from 17-Aug-15 to 25-Aug-15]																											
MAR12280	Zone D - Install Caisson Seawall 2C-L	3	26-Aug-15	28-Aug-15	[Gantt bar from 26-Aug-15 to 28-Aug-15]																											

Data Date: 30-Jun-15

- ◆ Current Milestone
- ▼ Current Milestone
- Actual Work
- Critical Remaining Work
- Remaining Work
- Remaining Level of Effort

**Works Programme for Non-CRIII Zones (June to August 2015)**

Date	Revision	Checked	Approved
03-Jul-15			







Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Schedule																																																																				
					June 2015	July 2015	August 2015	September 2015	October 2015	November 2015	December 2015	January 2016	February 2016	March 2016	April 2016	May 2016	June 2016	July 2016	August 2016	September 2016																																																					
					01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	01	08	15	22	29	06	13	20	27	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19
<b>CWB D - Slip Road 1 - Dwall Construction &amp; Piling</b>																																																																									
SIIA12260	Sec II A - CWB SR1: ground pre-treatment	27	17-Jan-15 A	31-Jul-15	[Gantt bar from 17-Jan-15 to 31-Jul-15]																																																																				
SIIA12280	Sec II A - CWB SR1: Guide Wall	30	10-Feb-15 A	08-Aug-15	[Gantt bar from 10-Feb-15 to 08-Aug-15]																																																																				
SIIA12305	Sec II A - CWB SR1: construct Permanent DWall (1.2m thk)	58	07-Apr-15 A	05-Sep-15	[Gantt bar from 07-Apr-15 to 05-Sep-15]																																																																				
SIIA12310	Sec II A - CWB SR1: construct pre-bored H-pile	42	19-Aug-15	08-Oct-15	[Gantt bar from 19-Aug-15 to 08-Oct-15]																																																																				
SIIA12320	Sec II A - CWB SR1: Temp. Cut-off Wall at Both Ends	45	15-Aug-15	08-Oct-15	[Gantt bar from 15-Aug-15 to 08-Oct-15]																																																																				
SIIA12340	Sec II A - CWB SR1: Ground treatment to Stop End (MTR CWL)	32	29-Aug-15	07-Oct-15	[Gantt bar from 29-Aug-15 to 07-Oct-15]																																																																				
<b>CWB D - Slip Road 1 - Pumping Test Preparation/ Pumping Test</b>																																																																									
SIIA12360	Sec II A - CWB SR1: Grout curtain / contact grout for Dwall	38	17-Aug-15	30-Sep-15	[Gantt bar from 17-Aug-15 to 30-Sep-15]																																																																				
SIIA12380	Sec II A - CWB SR1: Dwall sonic test / interface core	38	17-Aug-15	30-Sep-15	[Gantt bar from 17-Aug-15 to 30-Sep-15]																																																																				
SIIA12400	Sec II A - CWB SR1: Install dewatering/ recharging/ observation wells	38	24-Aug-15	08-Oct-15	[Gantt bar from 24-Aug-15 to 08-Oct-15]																																																																				
<b>Section III - Road D11 &amp; Part of Road P2, Area 4, Implement 1st Stage ITA</b>																																																																									
<b>Roadwork &amp; Utilities</b>																																																																									
<b>General</b>																																																																									
SIII10040	Sec III - roadwork & utilities - storm water drain & subsoil drain	121	01-May-15 A	21-Nov-15	[Gantt bar from 01-May-15 to 21-Nov-15]																																																																				
SIII10060	Sec III - roadwork & utilities - Watermain & Irrigation Mains	100	07-Jul-15*	03-Nov-15	[Gantt bar from 07-Jul-15 to 03-Nov-15]																																																																				
SIII10080	Sec III - roadwork & utilities - gas main and valve chamber	100	17-Jul-15	13-Nov-15	[Gantt bar from 17-Jul-15 to 13-Nov-15]																																																																				
SIII10100	Sec III - roadwork & utilities - HEC cable duct and catchpit	100	27-Jul-15	23-Nov-15	[Gantt bar from 27-Jul-15 to 23-Nov-15]																																																																				
SIII10120	Sec III - roadwork & utilities - sub-base	100	06-Aug-15	03-Dec-15	[Gantt bar from 06-Aug-15 to 03-Dec-15]																																																																				
SIII10140	Sec III - roadwork & utilities - Road kerb	100	15-Aug-15	12-Dec-15	[Gantt bar from 15-Aug-15 to 12-Dec-15]																																																																				
SIII10160	Sec III - roadwork & utilities - flexible pavement	100	26-Aug-15	23-Dec-15	[Gantt bar from 26-Aug-15 to 23-Dec-15]																																																																				
SIII10180	Sec III - roadwork & utilities - Road Lighting, TCSS Ducts & Traffic Signs	100	26-Aug-15	23-Dec-15	[Gantt bar from 26-Aug-15 to 23-Dec-15]																																																																				
<b>Section VI A - Box Culvert La, L1 &amp; FRP-L Construction</b>																																																																									
<b>Sec VI C - Box Culvert La bay 4 (North)</b>																																																																									
CUL11652	Sec VI C - Culvert L - bay 4 (north half) - excavate to formation level	18	25-Jul-15	14-Aug-15	[Gantt bar from 25-Jul-15 to 14-Aug-15]																																																																				
CUL11655	Sec VI C - Culvert L - bay 4 (north half) - place granular fill and lay geotextile filter	10	15-Aug-15	26-Aug-15	[Gantt bar from 15-Aug-15 to 26-Aug-15]																																																																				
<b>Box Culvert L1 &amp; FRP-L Construction (Bay 5 - Bay 7)</b>																																																																									
<b>Box Culvert L1 &amp; FRP-L - Bay 5 to 7 Structure</b>																																																																									
<b>Box Culvert L1 &amp; FRP-L - Precast Unit Fabrication (Pile Cap)</b>																																																																									
CUL10866	Sec VI C - Culvert L - bay 5-7 - PC1 to PC6 Construct precast Pile Cap	13	02-Jun-15 A	15-Jul-15	[Gantt bar from 02-Jun-15 to 15-Jul-15]																																																																				
<b>Box Culvert L1 &amp; FRP-L - Precast Unit Fabrication (Box Structure)</b>																																																																									
CUL10870	Sec VI C - Culvert L - bay 5, 6 & 7 - Construct precast culvert units with Bulkhead	17	18-Apr-15 A	20-Jul-15	[Gantt bar from 18-Apr-15 to 20-Jul-15]																																																																				
CUL10872	Sec VI C - Culvert L - bay 4b - Construct precast culvert units with Bulkhead	16	16-Jul-15	03-Aug-15	[Gantt bar from 16-Jul-15 to 03-Aug-15]																																																																				
CUL10873	Sec VI C - Culvert L - bay 4b, 5-7 - dismantle formwork and curing for precast culvert units	8	04-Aug-15	12-Aug-15	[Gantt bar from 04-Aug-15 to 12-Aug-15]																																																																				
<b>Box Culvert L1 &amp; FRP-L - Precast Unit Installation</b>																																																																									
CUL10864	Sec VI C - Culvert L - bay 5-7 - Demolition of Piling Platform	9	30-May-15 A	10-Jul-15	[Gantt bar from 30-May-15 to 10-Jul-15]																																																																				
CUL10865	Sec VI C - Culvert L - bay 5-7 - Install precast pile caps PC1 to PC6	12	11-Jul-15	24-Jul-15	[Gantt bar from 11-Jul-15 to 24-Jul-15]																																																																				
CUL10874	Sec VI C - Culvert L - bay 5-7 - Demolition of Temp Platform & Cofferdam ready for towing precast culvert	16	25-Jul-15	12-Aug-15	[Gantt bar from 25-Jul-15 to 12-Aug-15]																																																																				
CUL10875	Sec VI C - Culvert L - bay 5-7 (& Bay 4b) - install precast culvert units & Touch Up	16	13-Aug-15	31-Aug-15	[Gantt bar from 13-Aug-15 to 31-Aug-15]																																																																				
<b>Box Culvert L1 &amp; FRP-L - Bay 8</b>																																																																									




Activity ID	Activity Name	Remaining Dur	Early Start	Early Finish	Schedule																																																																				
					June 2015	July 2015	August 2015	September 2015	October 2015	November 2015	December 2015	January 2016	February 2016	March 2016	April 2016	May 2016	June 2016	July 2016	August 2016	September 2016																																																					
					01	08	15	22	29	06	13	20	27	03	10	17	24	31	07	14	21	28	05	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	01	08	15	22	29	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	04	11	18	25	01	08	15	22	29	05	12	19
<b>Box Culvert L1 &amp; FRP-L - Bay 8 Temp Work &amp; ELS</b>																																																																									
CUL10200	Culvert L - bay 8 - ELS and bulk excavation & Dwall Break Through ready for Flow Diversion	17	15-Jun-15 A	20-Jul-15																																																																					
<b>Box Culvert L1 &amp; FRP-L - Bay 9 to 11</b>																																																																									
<b>Box Culvert L1 &amp; FRP-L - Bay 9 to 11 General</b>																																																																									
CUL11695	Culvert L - [Summary of Cul L bay 9 to 11] - construct in-situ box culverts	17	08-Jun-15 A	20-Jul-15																																																																					
<b>Box Culvert L1 &amp; FRP-L - Bay 9</b>																																																																									
CUL11740	Culvert L - bay 9 - construct Wall & Roof	14	18-Jun-15 A	16-Jul-15																																																																					
<b>Box Culvert L1 &amp; FRP-L - Bay 10</b>																																																																									
CUL11860	Culvert L - bay 10 - construct Wall & Roof	17	30-Jun-15	20-Jul-15																																																																					
<b>Box Culvert L1 &amp; FRP-L - Bay 11</b>																																																																									
CUL11920	Culvert L - bay 11 - construct top slab	12	22-Jun-15 A	14-Jul-15																																																																					
<b>Box Culvert L1 &amp; FRP-L - Bay 9-11 Others</b>																																																																									
CUL11930	Culvert L - bay 9-11 - Upstand Wall	18	20-Jun-15 A	27-Jul-15																																																																					
CUL11940	Culvert L - bay 9-11 - divert flow to Culvert L permanent structures (bay 9 to bay 11)	0		31-Jul-15																																																																					
CUL12020	Culvert L - bay 9-11 - backfill from top slab to final formation level	60	28-Jul-15	07-Oct-15																																																																					
<b>Box Culvert L1 &amp; FRP-L - Bay 12 to 13</b>																																																																									
<b>Box Culvert L1 &amp; FRP-L - Bay 12 to 13 Piling</b>																																																																									
CUL12354	Culvert L - bay 12 - construct pre-bored H-pile (PC9)	12	27-Jun-15 A	14-Jul-15																																																																					
<b>Box Culvert L1 &amp; FRP-L - Bay 12 to 13 Temp Work &amp; ELS</b>																																																																									
CUL12385	Culvert L - bay 12 - ELS and bulk excavation & Dwall Break Through Ready for Diversion	23	03-Jun-15 A	27-Jul-15																																																																					
CUL12405	Culvert L - bay 12 & 13 - extract sheet piles ready for flow diversion (from Bay 4 to Bay 11)	5	27-Jul-15	31-Jul-15																																																																					
<b>Section VI C - Area 3, 6, 8A &amp; 8C</b>																																																																									
<b>Area 8A &amp; 8C - Seawall Modification</b>																																																																									
<b>Modification of Seawall</b>																																																																									
<b>Modification of Seawall - Zone 1 &amp; 2</b>																																																																									
PRS10043	Sec VIC - Pipe Pile P32 to P62	35	30-May-15 A	10-Aug-15																																																																					
PRS10044	Sec VIC - P33, P33A, P34, P34A, P35, P35A	24	11-Aug-15	07-Sep-15																																																																					
<b>Modification of Seawall - Zone 4</b>																																																																									
PRS10160	Sec VIC - Working Platform (Zone 4)	8	11-Aug-15	19-Aug-15																																																																					
PRS10180	Sec VIC - Pipe Pile P63 to P68 & P64A (Zone 4)	18	20-Aug-15	09-Sep-15																																																																					
<b>Area 6 - Box Culvert bay 5-6</b>																																																																									
SVIC10000	Sec VI C - [Summary] Construct Box Culvert Bay 5-6	53	18-Apr-15 A	31-Aug-15																																																																					
<b>Area 3 - Box Culvert bay 4 and Roadwork</b>																																																																									
SVIC10220	Sec VI C - [Summary] Construct Box Culvert Bay 4 in Area 3	53	01-Jan-15 A	31-Aug-15																																																																					
<b>Section VI D - Area 8B &amp; 10</b>																																																																									
<b>WDII Box 1 Construction</b>																																																																									
<b>WDII Box 1 Submission and Approval / Material Procurement</b>																																																																									
PCU60410	Sec VI D - WD II Box 1 - Prepare Subcontract for Box 1 structure	60	08-Aug-15	06-Oct-15																																																																					
<b>Section VII - Remainder Works</b>																																																																									
<b>Landing Steps Construction</b>																																																																									



Activity ID	Activity Name	Original Duration	Start	Finish	2015											
					May			Jun			Jul			Aug		
<b>DWP-06 (A) - Update Progress As of 20 May 15</b>																
<b>Works in TS3</b>																
<b>Works in TS3-East</b>																
<b>Diaphragm Wall</b>																
<b>TS3-East Post D/wall Works</b>																
TS3E_4100	D/wall Interface coring + grouting	60	20-Feb-15 A	29-May-15	D/wall Interface coring + grouting											
TS3E_4110	D/wall coring + fissure grouting	60	30-Mar-15 A	24-May-15	D/wall coring + fissure grouting											
TS3E_4120	D/wall integrity test	60	30-Mar-15 A	20-May-15 A	D/wall integrity test											
TS3E_4130	Dewatering & observation well installation	36	07-Apr-15 A	20-May-15 A	Dewatering & observation well installation											
TS3E_4140	Pumping test	7	07-May-15 A	20-May-15 A	Pumping test											
<b>ELS</b>																
<b>ELS Fabrication Works</b>																
TS3E_5510	ELS struts & waling fabrication	72	12-Mar-15 A	23-May-15	ELS struts & waling fabrication											
<b>TS3-East ELS Works</b>																
TS3E_5520	ELS Layer 1 - Soft Excav + Strut installation	12	02-May-15 A	29-May-15	ELS Layer 1 - Soft Excav + Strut installation											
TS3E_5540	ELS Layer 2 - Soft Excav + Strut installation	12	30-May-15	10-Jun-15	ELS Layer 2 - Soft Excav + Strut installation											
TS3E_5560	ELS Layer 3 - Soft Excav + Strut installation	12	11-Jun-15	22-Jun-15	ELS Layer 3 - Soft Excav + Strut installation											
TS3E_5580	ELS Layer 4 - Soft Excav + Strut installation	12	23-Jun-15	04-Jul-15	ELS Layer 4 - Soft Excav + Strut installation											
TS3E_5600	ELS Layer 5 - Soft Excav + Strut installation	12	05-Jul-15	16-Jul-15	ELS Layer 5 - Soft Excav + Strut installation											
TS3E_5620	ELS Layer 6 - Soft Excav + Strut installation	12	17-Jul-15	28-Jul-15	ELS Layer 6 - Soft Excav + Strut installation											
TS3E_5660	ELS Layer 7 - Soft Excav + Strut installation	10	29-Jul-15	07-Aug-15	ELS Layer 7 - Soft Excav + Strut installation											
TS3E_5670	Excavation up to Formation Level (No Rock as Rock Head Level is far below F.L.)	6	08-Aug-15	13-Aug-15	Excavation up to Form											
<b>Cut &amp; Cover Tunnel Structure</b>																
<b>Temporary Works Design</b>																
TS3E_2080	(01) RC Temp Work Design - submission	24	20-May-15 A	01-Jun-15	(01) RC Temp Work Design - submission											
TS3E_2085	(01) RC Temp Work Design - review and approval by AECOM	24	02-Jun-15	30-Jun-15	(01) RC Temp Work Design - review and approval by AECOM											
<b>Method Statement</b>																
TS3E_2090	(01)RC works method statement - submission	24	02-Jul-15	29-Jul-15	(01)RC works method statement - submission											
TS3E_2095	(01)RC works method statement - review and approval by AECOM	24	30-Jul-15	26-Aug-15	(01)RC works method statement - review and approval by AECOM											
<b>TS3-East CCT - Ch.4500.000 to Ch.4582.140</b>																
<b>TS3 East CCT - Blinding + Waterproofing</b>																
TS3E_6505	Commence CCT Works	0	14-Aug-15		◆ Commence CCT W											
<b>Removal of Reclamation</b>																
<b>Method Statement</b>																
TS3E_2100	(01) Removal of reclamation method statement - submission	24	14-Aug-15	10-Sep-15												
<b>Works in TS3-West</b>																
<b>Diaphragm Wall</b>																
<b>TS3-West Pre-D/wall Works</b>																
TS3W_2540	Guidewall construction	106	11-Feb-15 A	15-Jun-15	Guidewall construction											
TS3W_2530	Curtain grout/soil pre-treatment/slurry wall	137	12-Feb-15 A	16-Jun-15	Curtain grout/soil pre-treatment/slurry wall											
TS3W_2520A	Pre-drilling / Ground Investigation (SI) - Phase 2	107	09-Apr-15 A	10-Jun-15	Pre-drilling / Ground Investigation (SI) - Phase 2											
<b>TS3-West Diaphragm Construction</b>																

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-May-15	Updated to 20th May 2015	DML/WC	

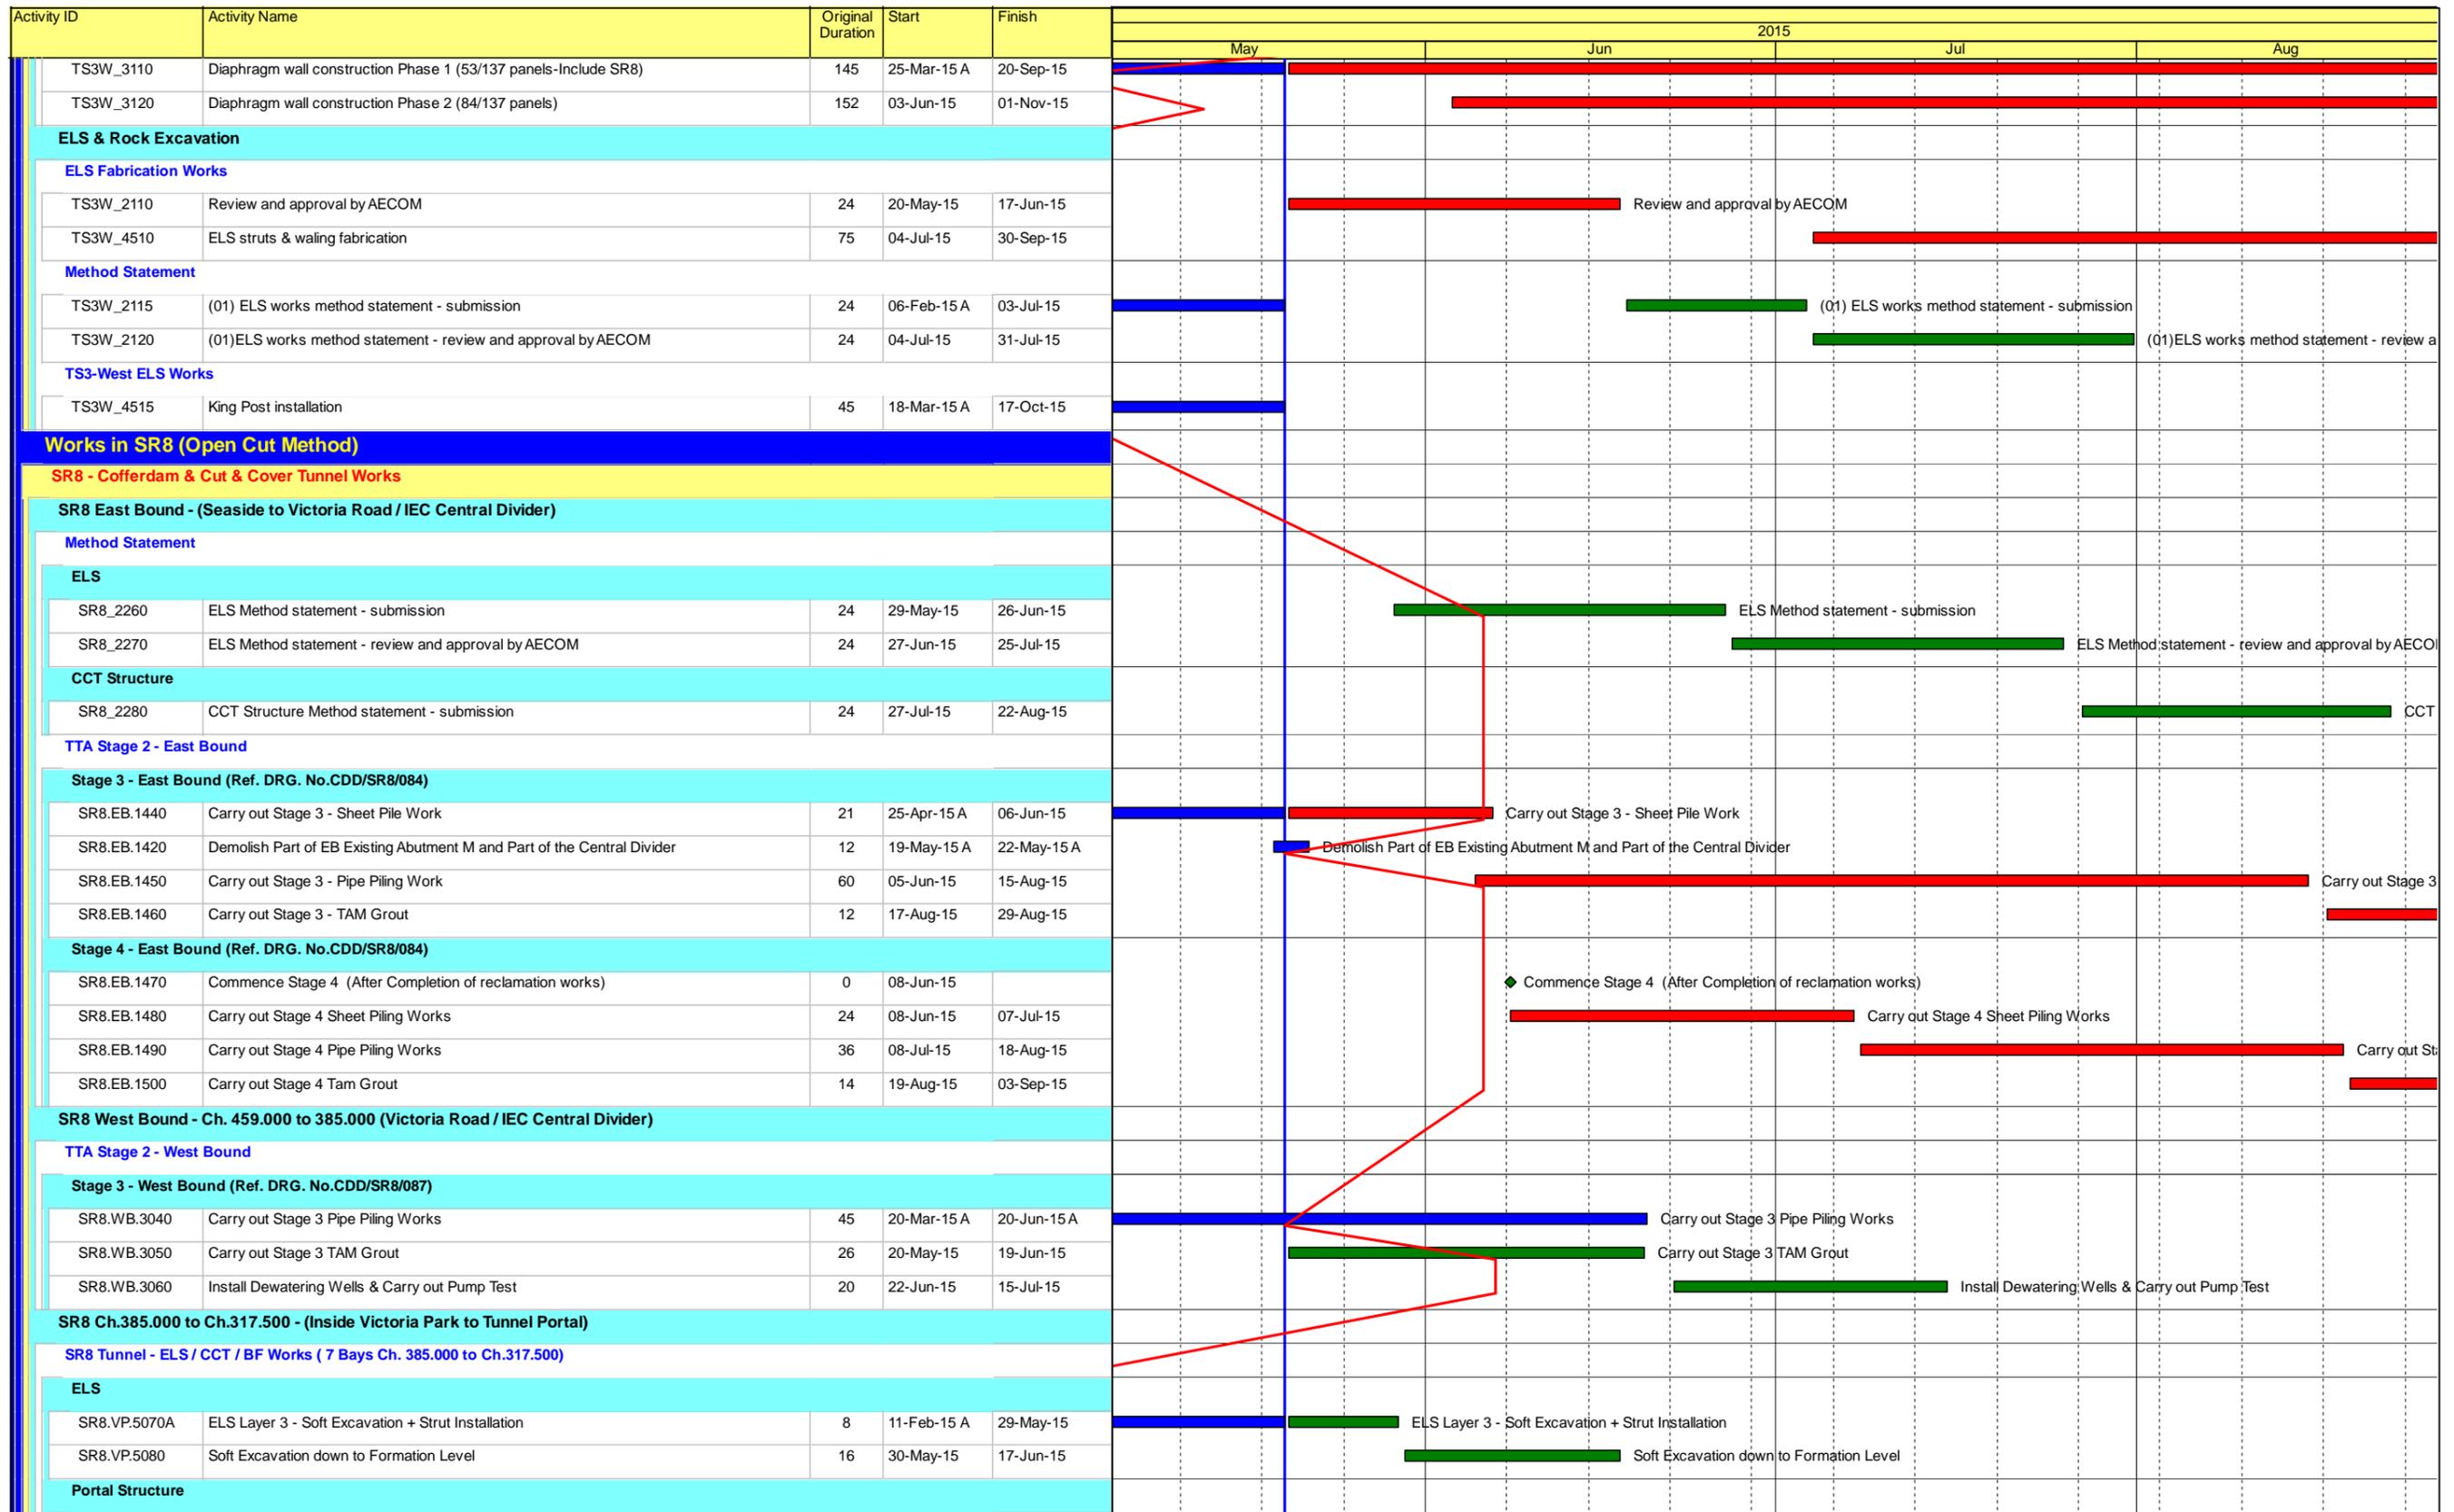

- █ Actual Work
- █ Remaining Work
- █ Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-May-15	Updated to 20th May 2015	DML/WC	

Activity ID	Activity Name	Original Duration	Start	Finish	2015				
					May	Jun	Jul	Aug	
<b>Blinding + Waterproofing</b>									
SR8.VP.5030	Blinding for Bay 1 to Bay 7	7	17-Jun-15	26-Jun-15					
SR8.VP.5090	Waterproofing for Bay 1 to Bay 7	7	27-Jun-15	06-Jul-15					
<b>Base Slab + Drainage</b>									
SR8.VP.5100	Base Slab - Bay 1	8	07-Jul-15	15-Jul-15					
SR8.VP.5110	Base Slab - Bay 2	8	16-Jul-15	24-Jul-15					
SR8.VP.5120	Base Slab - Bay 3	8	25-Jul-15	03-Aug-15					
SR8.VP.5130	Base Slab - Bay 4	8	04-Aug-15	12-Aug-15					
SR8.VP.5140	Base Slab - Bay 5	8	13-Aug-15	21-Aug-15					
<b>Pump Sump E</b>									
SR8.VP.5360	Base Slab	8	07-Jul-15	15-Jul-15					
SR8.VP.5370	Wall Up to Portal Base Slab Bottom	10	16-Jul-15	27-Jul-15					
SR8.VP.5380	Fill Up Void Up to Portal Base Slab Bottom	7	28-Jul-15	04-Aug-15					
<b>SR8 Ch 317.500 to Ch 210.000 - U-Structure &amp; Slab (Victoria Park)</b>									
<b>Excavation and Lateral Support</b>									
SR8_2310	ELS - Excavation to Formation Level + Lateral Support for UBA2 to UBA5	21	12-May-15 A	01-Jun-15					
<b>RC CCT &amp; Backfill Ch317.5000 to Ch240.000</b>									
<b>Structure</b>									
<b>Blinding + Waterproofing</b>									
SR8_1830	Blinding & Waterproofing Bay UBA2 to UBA5	4	02-Jun-15	05-Jun-15					
SR8_1840	Remove Bulk Head at CH317.5	7	18-Jun-15	26-Jun-15					
SR8_1860	Blinding & Waterproofing Bay UBA8	4	27-Jun-15	02-Jul-15					
<b>Base Slab</b>									
SR8_1810	SR8 U-structure Base slab (UBA2 - UBA5)	48	06-Jun-15	03-Aug-15					
SR8_1812	SR8 U-structure Base slab (UBA8)	24	03-Jul-15	30-Jul-15					
SR8_1813	Remove SL3 - (UBA8)	14	31-Jul-15	15-Aug-15					
SR8_1811	Remove SL2 - (UBA2 - UBA5)	28	04-Aug-15	04-Sep-15					
<b>Wall</b>									
SR8_1850B	SR8 U-structure Wall (UBA6-UBA7) - Stage 2	14	23-Feb-15 A	23-Jun-15					
SR8_1850A	Remove SL2, 1 (UBA6-UBA7)	14	20-May-15	05-Jun-15					
SR8_2060	SR8 U-structure Wall (UBA8) - Stage 1	7	17-Aug-15	24-Aug-15					
<b>Tsing Fung St - RW &amp; Subway Extension &amp; Toe Wall at Hing Fat St</b>									
<b>Ret. Wall &amp; TF Subway Extension (Portion V)</b>									
<b>Retaining Wall RW8C at Tsing Fung Street (Portion V)</b>									
VP_1770	Install Steel Railing on Top of RW8C	14	20-May-15	05-Jun-15					
VP_1390	Demolish Top Portion of Existing Wall Head and Kerb	18	05-Jun-15	27-Jun-15					
VP_1400	Road Formation - Subbase + Kerb + U-shape Channel	48	27-Jun-15	24-Aug-15					
<b>Retaining Wall + Toe Wall at Hing Fat Street</b>									
<b>Subway Extension at Tsing Fung Street (Portion VIII)</b>									
<b>West Side</b>									
VP_1365	Excavation and Demolition (West Part) of Subway	14	09-Apr-15 A	23-May-15					
VP_1375.10	TFS Subway extension - Blinding and Waterproofing	8	26-May-15	03-Jun-15					
VP_1375.20	TFS Subway extension - Base slab + Drainage	21	04-Jun-15	29-Jun-15					

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-May-15	Updated to 20th May 2015	DML/WC	

Activity ID	Activity Name	Original Duration	Start	Finish	2015				
					May	Jun	Jul	Aug	
VP_1375.30	TFS Subway extension - Walls	18	30-Jun-15	21-Jul-15					TFS Subway extension - Walls
VP_1375.40	TFS Subway extension - Roof Slab	14	22-Jul-15	06-Aug-15					TFS Subway extension - Roof Slab
VP_1375.70	Remove Soffit formwork for Roof Slab	32	07-Aug-15	12-Sep-15					
<b>RC Works - Toe Wall (RW8E)</b>									
VP_6152	Construct and divert Temporary Footpath	36	20-May-15	03-Jul-15					Construct and divert Temporary Footpath
VP_6160	Sheet Piling and Excavation to Formation level	45	04-Jul-15	25-Aug-15					
<b>Protection Works for IEC Abutment M</b>									
<b>TTA (Submissions, Approvals and Implementation)</b>									
ABUTM_0910	Preparation and submission	36	06-Jul-15	15-Aug-15					Preparation and s
ABUTM_0915	TMLG - review and approval	24	17-Aug-15	12-Sep-15					
<b>Design Submissions</b>									
ABUTM_0945	Prepare Shop Drawings for Temporary Works	24	06-Jul-15	01-Aug-15					Prepare Shop Drawings for Temporary Wo
ABUTM_0955	Engineer's Review and Approval - Temp Works	24	03-Aug-15	29-Aug-15					
ABUTM_0965	Prepare Shop Drawings for Permanent Works	24	03-Aug-15	29-Aug-15					
<b>Method Statement</b>									
ABUTM_0900	(01)Protection works method statement - submission	24	03-Aug-15	29-Aug-15					
<b>Works in Victoria Park</b>									
<b>Re-Provisioning Works</b>									
<b>Pavilion</b>									
<b>Materials Submission</b>									
VP_6660	Issue P.O. / Manufacturing / Fabrication	48	29-Apr-15 A	06-Jun-15					Issue P.O. / Manufacturing / Fabrication
<b>Shop Drawings</b>									
VP_0215	Shopdrawing - ER review and approval	24	13-Apr-15 A	23-May-15					Shopdrawing - ER review and approval
<b>Method Statement</b>									
VP_6690	(01)Method statement - review and approval by AECOM	24	20-Apr-15 A	27-May-15					(01)Method statement - review and approval by AECOM
<b>Construction Works - BG Pavillion</b>									
VP_1300	PV - Initial works (Site Clearance, underground utilities etc.)	24	09-Apr-15 A	12-Jun-15					PV - Initial works (Site Clearance, underground utilities etc.)
VP_1340	Demolish existing BGO	24	20-May-15 A	10-Jun-15					Demolish existing BGO
VP_1360	PV - foundation works	21	30-May-15	24-Jun-15					PV - foundation works
VP_1380	PV- structural works, G/F to Roof	24	22-Jun-15	20-Jul-15					PV- structural works, G/F to Roof
VP_1420	PV - ABWF	36	21-Jul-15	31-Aug-15					
VP_1430	PV - E&M Works	36	28-Jul-15	07-Sep-15					
<b>Bowling Green</b>									
<b>Design Submissions for Bowling Green Lighting</b>									
VP_0330	Engineer's Review and Approval	24	23-Sep-14 A	21-May-15					Engineer's Review and Approval
<b>Procurement</b>									
VP_1010.184	Issue PO / Manufacturing	10	22-May-15	03-Jun-15					Issue PO / Manufacturing
VP_1010.194	Delivery	11	04-Jun-15	16-Jun-15					Delivery
VP_6670	Materials Delivery - Green Turf	24	08-Jun-15	07-Jul-15					Materials Delivery - Green Turf
<b>Construction Works</b>									
VP_1170	Demolish existing CP / BGO / Site Clearance	24	09-Apr-15 A	20-May-15					Demolish existing CP / BGO / Site Clearance
VP_1710	BG - Install U/G Sewerage System	24	29-Apr-15 A	02-Jun-15					BG - Install U/G Sewerage System
VP_1720	BG - Install Drainage System	24	20-May-15	17-Jun-15					BG - Install Drainage System

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆ Milestone

Date	Revision	Checked	Approved
20-May-15	Updated to 20th May 2015	DML/WC	

Activity ID	Activity Name	Original Duration	Start	Finish	2015																			
					May	Jun	Jul	Aug																
VP_1730	BG - Install Irrigation System	24	04-Jun-15	03-Jul-15																				
VP_1740	BG - Install Conduit and Lighting System	36	18-Jun-15	31-Jul-15																				
VP_1450	BG - Re-provisioning works - Hardscape & Furnitures (Green Turf/ Granite Tiles)	36	15-Jul-15	25-Aug-15																				
VP_1745	Test & Commission - Lighting System	16	01-Aug-15	19-Aug-15																				
<b>Mooring Components Upkeep (CBTS and ATS)</b>																								
MAR_2000	Mooring Upkeep at Portion XIX(19) & XX(20) - ATS (if instructed by Engineer)	1399	21-Mar-13 A	17-Jan-17																				
MAR_1000	Mooring Upkeep at Portion III (3) - CBTS	574	15-May-14 A	09-Dec-15																				
MAR_3020	Mooring Upkeep at Portion X(10) & XVI(16) - CBTS	979	15-May-14 A	21-Jan-17																				
<b>Works for Public Works Regional Laboratory (North Lantau)</b>																								
<b>Maintenance and Upkeep of New PWRL (Portion XVII)</b>																								
PWRL_1050	Maintenance/ Upkeep of New PWRL	1301	19-Jul-13 A	21-Nov-17																				

- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone

Date	Revision	Checked	Approved
20-May-15	Updated to 20th May 2015	DML/WC	
