



東業德勤測試顧問有限公司
ETS-TESTCONSULT LTD.TM

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: etl@ets-testconsult.com
W: www.ets-testconsult.com

ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE

*CONTRACT NO. DC/2013/10 - DESIGN,
BUILD AND OPERATE SAN WAI
SEWAGE TREATMENT WORKS –
PHASE 1*

**MONTHLY EM&A REPORT
NO. 2**

(01 JUNE – 30 JUNE 2017)

Prepared by: _____

LO, Ting Yi

Certified by: _____

LAU, Chi Leung
Environmental Team Leader

Issued Date: 11 July 2017

Report No.: ENA74112

This report shall not be reproduced unless with prior written approval from this laboratory.



Drainage Services Department
Sewage Services Branch
Harbour Area Treatment Scheme
5/F, Western Magistracy
2A Po Fu Lam Road
Hong Kong

Your reference:

Our reference: HKDSD203/50/104474

Date: 8 August 2017

Attention: Ms Carol Ho

BY EMAIL & POST
(email: carolho@dsd.gov.hk)

Dear Sirs

Agreement No. HATS 02/2016
Services for Independent Environmental Checker (IEC) for
Contract No. DC/2013/10 – Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Monthly Environmental Monitoring and Audit Report No.2 (June 2017)

We refer to emails of 11, 13, 15 July and 7 August 2017 from ETS-Testconsult Limited attaching the Monthly Environmental Monitoring and Audit Report No.2 (June 2017).

We have no further comment and hereby verify the Monthly Environmental Monitoring and Audit Report No.2 (June 2017) in accordance with Clause 5.4 of the Environmental Permit no. EP-464/2013.

Should you have any queries, please do not hesitate to contact the undersigned or our Mr Nic Lam on 2618 2836.

Yours faithfully
ANewR CONSULTING LIMITED

Adi Lee
Independent Environmental Checker

LYMA/LHHN/WCKJ/lhnh

cc AECOM – Mr Patrick Leung (email: patrick.leung@swstw-aecom.com)
ETS-Testconsult Limited – Mr C L Lau (email: env@ets-testconsult.com)

TABLE OF CONTENTS

EXECUTIVE SUMMARY

1	INTRODUCTION	1-2
1.1	Basic Project Information	1
1.2	Project Organization	2
1.3	Construction Programme	2
1.4	Construction Works Undertaken During the Reporting Period	2
2	AIR QUALITY MONITORING	3-7
2.1	Monitoring Requirements	3
2.2	Monitoring Equipment	3-4
2.3	Monitoring Parameters, Frequency and Duration	4-5
2.4	Action and Limit Levels	5
2.5	Results and Observations	5
2.6	Event and Action Plan	5-7
3	NOISE MONITORING	7-11
3.1	Monitoring Requirements	8
3.2	Monitoring Equipment	8
3.3	Monitoring Duration and Frequency	8
3.4	Monitoring Locations	8
3.5	Monitoring Methodology	9
3.6	Actions and Limit Level	9
3.7	Results and Observation	9
3.8	Event and Action Plan	10-11
4	WATER QUALITY MONITORING	11-16
4.1	Monitoring Requirements	11
4.2	Monitoring Methodology and Equipment	11
4.3	Monitoring Frequency	12
4.4	Quality Assurance (QA) / Quality Control (QC)	12
4.5	Action and Limit Levels	12-13
4.6	Result and Observation	13
4.7	Event and Action Plan	13-16
5	ENVIRONMENTAL SITE INSPECTION AND AUDIT	16-21
5.1	Site Inspection	16-17
5.2	Advice on the Solid and Liquid Waste Management Status	17-18
5.3	Discharge License and Results of Effluent Monitoring	18
5.4	Environmental Licenses and Permits	18
5.5	Implementation Status of Environmental Mitigation Measures	18-20
5.6	Summary of Exceedance of the Environmental Quality Performance Limit	20
5.7	Summary of Complaints, Notification of Summons and Successful Prosecution	20-21
6	FUTURE KEY ISSUES	21-22
6.1	Construction Programme for the Coming Months	21
6.2	Key Issues for the Coming Month	21-22
6.3	Environmental Monitoring and Site Inspection Schedule for the Coming Month	22
7	CONCLUSION	22
7.1	Conclusion	22

LIST OF TABLES

Table 1.1	Contact Information of Key Personnel
Table 2.1	Air Quality Monitoring Equipment
Table 2.2	Monitoring Parameters, Duration and Frequencies of Impact Air Quality Monitoring
Table 2.3	Time Schedule of Impact Air Quality Monitoring
Table 2.4	The criteria of Action and Limit Levels for Air Quality
Table 2.5	Action and Limit Levels for 1-hour TSP and 24-hour TSP
Table 2.6	Event and Action Plan for Air Quality (Dust) during Construction Phase
Table 3.1	Noise Monitoring Equipment
Table 3.2	Time Schedule of Impact Noise Monitoring
Table 3.3	Noise Monitoring Stations
Table 3.4	Action and Limit Levels for Noise Monitoring
Table 3.5	Event/Action Plan for Construction Noise
Table 4.1	Summary of Testing Procedures for water samples
Table 4.2	Monitoring Frequency of Water Quality Monitoring
Table 4.3	Time Schedule of Impact Water Quality Monitoring
Table 4.4	The criteria of Action and Limit Levels for Water Quality
Table 4.5	Action and Limit Levels for Water Quality
Table 4.6	Event and Action Plan for Water Quality
Table 5.1	Summary of observation of site inspections
Table 5.2	Summary of Quantities of Inert C&D Materials
Table 5.3	Summary of Quantities of C&D Materials
Table 5.4	Summary of Environmental Complaints Notification of Summons and Successful Prosecution

LIST OF APPENDICES

Appendix A	Location of Work Area
Appendix B	Project Organization Chart
Appendix C	Construction Programme
Appendix D1	Calibration Certificates for Impact Air Quality Monitoring Equipment
Appendix D2	Impact Air Quality Monitoring Results
Appendix D3	Graphical Plots of Impact Air Quality Monitoring Results
Appendix E1	Calibration Certificates for Impact Noise Monitoring Equipment
Appendix E2	Impact Noise Monitoring Results
Appendix E3	Graphical Plots of Impact Noise Monitoring Data
Appendix F1	Calibration Certificates for Impact Water Quality Monitoring Equipments
Appendix F2	Impact Water Quality Monitoring Results
Appendix F3	Graphical Plots of Impact Water Quality Monitoring Data
Appendix G	Weather Condition
Appendix H	Environmental Site Inspection Checklists
Appendix I	Waste Flow Table
Appendix J	Environmental Licenses and Permits
Appendix K	Implementation Schedule for Environmental Mitigation Measures (EMIS)
Appendix L	Environmental Site Inspection Schedule
Appendix M	Investigation Reports on Action Level or Limit Level Non-compliance
Appendix N	Laboratory Report for Discharge Water

FIGURES

Figure 1	Air Quality and Noise Monitoring Stations
Figure 2	Water Quality Monitoring Stations



EXECUTIVE SUMMARY

This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Stage 1 (the Project) (hereafter referred to as “the Contract”). The Contract was awarded to ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE (ADCJV) by the Drainage Services Department (DSD) and ETS-Testconsult Limited was appointed as the Environmental Team (ET) by ADCJV to implement the EM&A program in compliance with the EP and the EM&A Manuals.

According to the Section 25 of the Particular Specification (PS) and the Environmental Permit No. EP-464/2013, an EM&A programme should be implemented in accordance with the procedures and requirements in the EM&A Manual of the approved EIA report (Registration No. AEIAR-072/2003). The scope of monitoring works includes air quality, construction noise, water quality and environmental site audit.

Baseline monitoring was completed in April 2017. Action and Limit Levels were established for air quality, noise and water quality parameters based on the baseline monitoring results.

This is the second Monthly Environmental Monitoring and Audit (EM&A) Report for the Contract which summaries findings of the EM&A works conducted during the reporting period from 01 June 2017 to 30 June 2017.

Site Activities

As informed by the Contractor, site activities were carried out in this reporting month:

- *Piling Foundation (Prebored H-pile)*
- *Piling Foundation (Driven H-pile)*
- *Portion 5 (Access Road) Works*
- *Drainage Outlet connection (Effluent Connection to the Existing Junction Chamber)*
- *Diversion of Existing Street Lighting and Traffic Signs*
- *Civil Works by ADCJV for HyD's Diversion of Existing Street Lighting and Traffic Sign*
- *Civil Works by ADCJV for WSD's Diversion of Existing Watermains*
- *Civil Works by ADCJV between Site Boundary for WSD's Diversion of Existing Watermains*

Environmental Monitoring and Audit Progress

The monthly EM&A programme was undertaken in accordance with the EM&A Manual for this Contract. The summary of the monitoring activities in this reporting month is listed below:

- *24-hour TSP Monitoring: 5 Occasions at 2 designated locations*
- *1-hour TSP Monitoring: 15 Occasions at 2 designated locations*
- *Noise Monitoring (Day-time): 5 Occasion at 2 designated locations*
- *Water Quality Monitoring: 14 Occasions at 1 designated location*
- *Weekly Site inspection: 5 Occasions*

Air Quality Monitoring

No exceedance of Action and Limit levels was recorded for 1-hr and 24-hr TSP monitoring in the reporting month.

Noise Monitoring

No exceedance of Action and Limit levels for noise monitoring was recorded in the reporting month.

Water Quality Monitoring

According to the summary of water monitoring results, there was one limit level exceedance of suspended solid at station R1b on 13 June 2017. After investigation, there was concluded that the exceedance was not relevant to this Contract since there was no construction works conducted from 12:00noon on 12 June 2017 to 13:30pm on 13 June 2017 which was unlikely to generate suspended solid and thus deteriorate the water quality at the monitoring station R1b on 13 June 2017. Besides, Tropical Cyclone Warning Signal No.8 was hoisted from 12 to 13 June 2017 and Red Rainstorm Warning Signal was hoisted during water monitoring period on 13 June 2017 which would deteriorate the water quality at the monitoring station R1b on 13 June 2017. Indeed, a temporary storage pool was established in the lowest position of the construction site for acting as a prior sedimentation tank. The surface runoff was first stored in the temporary storage pool and then transferred to the Wetsep for proper treatment prior to discharge. The effluent was thus brought into an acceptable minimum level and also ensured to comply with the requirements specified in the discharge license. In addition, there was no water discharge in the morning of 13 June 2017. Thus, the exceedance of water samples taken from 11:38 to 11:49am on 13 June 2017 was considered as non-Project related. The Investigation Reports No. 001 (including the causes of exceedance, action taken and recommendation for mitigation) for Action or Limit Level Non-compliance were provided in **Appendix M**. Other than the above exceedance, no exceedance of Action and Limit level was recorded in the reporting month.

Weekly Site Inspections

In general, performance on environmental mitigation measures implemented was found to be satisfactory in this reporting month. The major findings observed during site inspections are presented in the **Section 5.0**.

Complaint Log

There was no complaint received in relation to the environmental impact during the reporting period.

Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during the reporting period.

Reporting Change

There were no reporting changes during the reporting period.

Future Key Issues

The future key issues to be undertaken in the upcoming month are as follows:

- *Piling Foundation (Prebored H-pile) for Chemically Enhanced Primary Treatment and Sludge Dewatering Building;*
- *Piling Foundation (Driven H-pile) for Inlet Work, Preliminary Treatment Works and Inlet Pumping Station;*
- *Piling Foundation (minipile);*
- *Portion 5 (Access Road) Works;*
- *Drainage Outlet connection (Effluent Connection to the Existing Junction Chamber);*
- *Diversion of Existing Street Lighting and Traffic Sign;*
- *Civil Works by ADCJV for HyD's Diversion of Existing Street Lighting and Traffic Signs;*
- *Civil Works by ADCJV for WSD's Diversion of Existing Watermains;*
- *Civil Works by ADCJV between Site Boundary for WSD's Diversion of Existing Watermains*

1. INTRODUCTION

1.1. Basic Project Information

- 1.1.1. This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Stage 1 (the Project) (hereafter referred to as “the Contract”). The Contract was awarded to ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE (ADCJV) by the Drainage Services Department (DSD) and ETS-Testconsult Limited was appointed as the Environmental Team (ET) by ADCJV to implement the EM&A program in compliance with the EP and the EM&A Manuals.
- 1.1.2. The project involves expansion of the preliminary treatment works at San Wai STW from 164,000 m³/d to 200,000 m³/d Average Dry Weather Flow, upgrading the preliminary treatment level to CEPT and adding centralized disinfection. The site layout plan is shown in **Appendix A**.
- 1.1.3. According to the Section 25 of the Particular Specification (PS) and the Environmental Permit No. EP-464/2013, an EM&A programme should be implemented by an independent Environmental Team (ET) in accordance with the procedures and requirements in the EM&A Manual of the approved EIA report (Registration No. AEIAR-072/2003). These documents are available through the EIA Ordinance Register. The construction works of the Contract commenced on 16 May 2017.
- 1.1.4. The scope of monitoring works includes air quality, construction noise, water quality and environmental site audit. The EM&A requirements for each parameter described in the following sections include:
- *All monitoring parameters;*
 - *Monitoring schedules for the reporting month and forthcoming months;*
 - *Action and Limit levels for all environmental parameters;*
 - *Event/Action Plans;*
 - *Environmental mitigation measures, as recommended in the Project EIA study final report; and*
 - *Environmental requirements in contract documents.*
- 1.1.5. As part of the project EM&A program, baseline monitoring was conducted from 21 March 2017 to 15 April 2017 to determine the ambient environmental conditions before the project commence any major construction works and it had been verified by IEC and endorsed by EPD.
- 1.1.6. This is the second Monthly Environmental Monitoring and Audit (EM&A) Report for the Contract which summaries the audit findings of the EM&A programme during the reporting period from 01 June to 30 June 2017.

1.2. Project Organization

1.2.1. The project organization structure and lines of communication with respect to the on-site environmental management structure is shown in **Appendix B**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name of Key Staff	Tel. No.	E-mail
Supervising Officer (AECOM Asia Co. Ltd.)	Resident Engineer	Mr. Patrick Leung	5222 6561	patrick.leung@swstw-aecom.com
Independent Environmental Checker (ANewR Consulting Limited)	Technical Director	Mr. Adi Lee	2618 2836	aymlee@anewr.com
	Senior Environmental Consultant	Mr. Nic Lam	2618 2836	nhhlam@anewr.com
Contractor (ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE)	Environmental Officer	Mr. Johnny So	9513 8899	johnny.so@c302.chechk.com
	Environmental Supervisor	Ms Cherry Ye	6237 1125	cherry.ye@c302.chechk.com
Environmental Team (ETS-Testconsult Ltd.)	Environmental Team Leader	Mr. C. L. Lau	2946 7791	env@ets-testconsult.com

1.3. Construction Programme

1.3.1. A copy of the Contractor's construction programme is provided in **Appendix C**.

1.4. Construction Works Undertaken During the Reporting Period

1.4.1. A summary of the construction activities undertaken during this reporting period is shown below:

- Piling Foundation (Prebored H-pile)
- Piling Foundation (Driven H-pile)
- Portion 5 (Access Road) Works
- Drainage Outlet connection (Effluent Connection to the Existing Junction Chamber)
- Diversion of Existing Street Lighting and Traffic Signs
- Civil Works by ADCJV for HyD's Diversion of Existing Street Lighting and Traffic Sign
- Civil Works by ADCJV for WSD's Diversion of Existing Watermains
- Civil Works by ADCJV between Site Boundary for WSD's Diversion of Existing Watermains

2. AIR QUALITY MONITORING

2.1. Monitoring Requirements

- 2.1.1. 1-hr and 24-hr TSP levels were monitored in the reporting month in accordance with the EM&A Manual. Two air monitoring location were selected which was shown in **Figure 1**.

2.2. Monitoring Equipment

1-hour TSP Monitoring

1-hour TSP levels were measured by using dust meter which are capable of producing comparable results as the by high volume sampling method, to indicate short event impacts. The dust meter is compliant to the clause 1.2.5 of "General Technical Requirement of Environmental Monitoring" and clause 2.2 of "Generic Environmental Monitoring and Audit Manual".

Table 2.1 summarized the dust meter model used during the baseline monitoring. Copies of calibration certificates for dust meters were attached in **Appendix D1**.

Table 2.1 Air Quality Monitoring Equipment

<i>Equipment</i>	<i>Model</i>
<i>Dust Meter</i>	<i>SIBATA LD-3B</i>
<i>High volume sampler (HVS)</i>	<i>Greasby GMW (GS2310)</i>
<i>Calibrator</i>	<i>Tisch TE-5025A</i>

1-hr air quality monitoring (Dust Meter)

Measuring Procedures

The measuring procedures of the dust meter are in accordance with the Manufacturer's instruction Manual as follows:

- Press POWER to ON, check the battery indicator to ensure whether the power supply is enough to conduct the TSP monitoring;
- Press TIMER SET to Manual;
- Press START/STOP SWITCH to start the TSP monitoring;
- Press START/STOP SWITCH to stop the TSP monitoring after monitoring complete;
- Record measured COUNT directly from the dust meter and calculate the TSP level by using the equation of the certificate.

Maintenance & Calibration (QA/QC)

- Dust meter should be checked at 3-month intervals and calibrated at half-year intervals throughout all stages of air quality monitoring.

24-hr air quality monitoring (HVS)

Instrumentation

High volume sampler, as HVS, (Greasby GMWS2310) complete with appropriate sampling inlets were employed for both 1-hour and 24-hour TSP monitoring. The sampler is composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complies with that required by USEPA standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

Installation

The installation of HVS refers to the requirement stated in EM&A Manual.

Operation/Analytical Procedures

Operating/analytical procedures for the operation of HVS are as below:

- Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 0.6m³/min and 1.7m³/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50. The flow rate was indicated on the flow rate chart.
- For TSP sampling, fiberglass filters (Whatman G653) were used.
- The power supply was checked to ensure the sampler worked properly.
- On sampling, the sampler was operated 5 minutes to establish thermal equilibrium before placing any filter media at designated air monitoring station.
- The filter holding frame was then removed by loosening the four nuts and carefully a weighted and conditioned filter was centered with the stamped number upwards, on a supporting screen.
- The filter was aligned on the screen so that the gasket formed an air-tight seal on the outer edges of the filter. Then the filter holder frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- The programmable timer will be set for a sampling month of 1 hour or 24 hours. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number.).
- After sampling, the filter was transferred from the filter holder of the HVS to a sealed plastic bag and sent to the laboratory for weighting. The elapsed time was also recoded.
- Before weighting, all filters were equilibrated in desiccators for 24 hour with the temperature of 25°C ± 3°C and the relative humidity (RH) <50% ±5%.

Maintenance & Calibration (QA/QC)

- HVS and their accessories should be maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVS should be calibrated at bi-monthly intervals.

Wind Data Monitoring

Wind data (wind speed and wind direction) were directly extracted from Wetland Park Station of Hong Kong Observatory. All wind data during this reporting month are shown in **Appendix G**.

2.3. Monitoring Parameters, Frequency and Duration

- 2.3.1. **Table 2.2** summarizes the monitoring parameters, monitoring duration and frequencies of impact air quality monitoring.

Table 2.2 Monitoring Parameters, Duration and Frequencies of Impact Air Quality Monitoring

<i>Parameter</i>	<i>Duration</i>	<i>Frequency</i>
1-hr TSP	1 hr (0800-1900)	Three times per 6 days
24-hr TSP	24 hr	Once per 6 days

- 2.3.2. In this reporting period, a total of 15 occasions of 1-hour TSP monitoring and 5 events of 24-hour TSP monitoring were undertaken and the schedule was shown in **Table 2.3**

Table 2.3 Time Schedule of Impact Air Quality Monitoring

June 2017						
<i>Sunday</i>	<i>Monday</i>	<i>Tuesday</i>	<i>Wednesday</i>	<i>Thursday</i>	<i>Friday</i>	<i>Saturday</i>
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17

18	19	20	21	22	23	24
25	26	27	28	29	30	

Remark: (▼) = Air quality monitoring carried out by ET.

2.4. Action and Limit Levels

The criteria for Action and Limit levels have been set out in the contract document of the Project as follows:

Table 2.4 The criteria of Action and Limit Levels for Air Quality

Parameters	Action	Limit
1-hour TSP Level ($\mu\text{g}/\text{m}^3$)	For baseline level $\leq 384\mu\text{g}/\text{m}^3$, Action level = (baseline level plus*1.3 + Limit Level) / 2	500 $\mu\text{g}/\text{m}^3$
	For baseline level $> 384\mu\text{g}/\text{m}^3$, Action level = Limit Level	
24-hour TSP Level ($\mu\text{g}/\text{m}^3$)	For baseline level $< 200\mu\text{g}/\text{m}^3$, Action level = (baseline level plus*1.3 + Limit Level) / 2	260 $\mu\text{g}/\text{m}^3$
	For baseline level $\geq 200\mu\text{g}/\text{m}^3$, Action level = Limit Level	

Following the criteria shown in **Table 2.4**, the Action and Limit levels for 1-hour TSP derived as illustrated in **Table 2.5**.

Table 2.5 Action and Limit Levels for 1-hour TSP and 24-hour TSP

Air Quality Monitoring Station	1-hr TSP ($\mu\text{g}/\text{m}^3$)		24-hr TSP ($\mu\text{g}/\text{m}^3$)	
	Action Level	Limit Level	Action Level	Limit Level
ASR1a	309	500	260	260
ASR2a	292	500	228	260

2.5. Results and Observations

2.5.1. 1-hour and 24-hour TSP Monitoring Results

Monitoring data of both 1-hour and 24-hour TSP monitoring carried out in this reporting month are summarized in **Appendix D2**. Graphical presentation of 1-hour and 24-hour TSP monitoring results for the reporting month is shown in **Appendix D3**. Wind data included wind speed and wind direction was extracted from Wetland Park Station of Hong Kong Observatory during this reporting month and is presented in **Appendix G**.

No exceedance of Action and Limit Level of 1-hr TSP and 24-hour TSP monitoring results was recorded during the reporting month.

2.5.2. Observation

Generally, 1-hour TSP and 24-hour TSP monitoring results fluctuated well below the Action Level in this reporting period. The major dust source observed near the monitoring stations was mainly from vehicles passing by the container yards and general earth works. It can be concluded that the contractor implemented sufficient dust mitigation measures during this reporting month.

2.6. Event and Action Plan

If the impact monitoring results exceed the Action and Limit Levels, the actions specified in **Table 2.6** shall be carried out.

Table 2.6 Event and Action Plan for Air Quality (Dust) during Construction Phase

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded for one sample	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Action Level being exceeded for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency to daily; 5. Discuss with IEC and Contractor on remedial actions required; 6. If exceedance continues, arrange meeting with IEC and ER; 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial actions to IEC within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
Limit Level being exceeded for one sample	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC, ER and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with Contractor on the possible mitigation measures; 3. Review the 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Check monitoring data and Contractor's working methods; 4. Discuss with IEC and 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to ER within 3 working days of notification; 3. Implement the agreed proposals;

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
	of Contractor's remedial actions; 6. Keep EPD and ER informed of the results.	proposed mitigation measures submitted by Contractor and advise the ER accordingly.	Contractor on potential remedial actions; 5. Ensure remedial actions properly implemented.	4. Amend proposal if appropriate.
Limit Level being exceeded for two or more consecutive samples	1. Identify source; 2. Inform IEC, ER and EPD the causes & actions taken for the exceedance s; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Investigate the causes of exceedance; 6. Arrange meeting with EPD and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with Contractor on the possible mitigation measures; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Supervise the implementation of mitigation measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 4. Discuss with IEC and the Contractor on potential remedial actions; 5. Review Contractor's remedial actions whenever necessary to assure their effectiveness; 6. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not resolved; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

3. NOISE MONITORING

3.1. Monitoring Requirements

- 3.1.1. Noise levels (L_{eq} , L_{10} and L_{90}) were monitored in the reporting month in accordance with the EM&A Manual.

3.2. Monitoring Equipment

Sound level meters used for impact noise monitoring were Type 1 sound level meters capable of giving a continuous readout of the noise level reading including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x). They complied with International Electro technical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 3.1** summarized the noise monitoring equipment model used during the baseline monitoring. Copies of calibration certificates for noise meters and calibrators were attached in **Appendix E1**.

Table 3.1 Noise Monitoring Equipment

Noise Monitoring Equipment	Model
Sound Level Meter	Rion NL-31 / Rion NL-52
Sound Level Calibrator	Rion NC-73 / Castle GA607

3.3. Monitoring Duration and Frequency

- 3.3.1. Impact noise monitoring for the A-weighted levels L_{eq} , L_{10} and L_{90} in 30-minute interval was recorded once per 6 days.
- 3.3.2. In this reporting period, a total of 5 occasions of noise monitoring were undertaken and the schedule was shown in **Table 3.2**

Table 3.2 Time Schedule of Impact Noise Monitoring

June 2017						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1	2	3
4	5	6 ▼	7	8	9	10
11	12 ▼	13	14	15	16	17 ▼
18	19	20	21	22	23 ▼	24
25	26	27	28	29 ▼	30	

Remark: (▼) = Noise monitoring carried out by ET.

3.4. Monitoring Locations

Two noise monitoring stations, NSR1a (晉榮貨櫃服務有限公司) and NSR2a (永康貨櫃服務有限公司) which shown in Figure 1, were required to perform impact noise monitoring.

The impact noise monitoring programme was summarized in **Table 3.3**.

Table 3.3 Noise Monitoring Stations

Noise monitoring station	Type of Measurement
NSR1a	Façade
NSR2a	Free Field

3.5. Monitoring Methodology

Instrumentation

Integrating Sound Level Meters were employed for noise monitoring.

Operation/Analysis Procedures

- The Sound Level Meter was set on a tripod at a height of 1.2m above the ground.
- For free field measurement, the meter was positioned away from any nearby reflective surfaces.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - Frequency weighting : A
 - Time weighting : Fast
 - Time measurement : 30 mins
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1000HZ. If the difference in the calibration level before and after measurement was more than 1 dB(A), the measurement would be considered invalid and repeat measurement would be required after re-calibration or repair of the equipment.
- During the monitoring period, the L_{eq} , L_{10} and L_{90} were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- 3dB(A) correction had been added to the results if noise measurements were free-field.
- Noise monitoring would be cancelled in the presence of fog, rain, storm, wind with a steady speed exceeding 5m/s, or wind gusts exceeding 10m/s.

Maintenance and Calibration (QA/QC)

- The microphone head of the sound level meter and calibrator are cleaned with soft cloth at quarterly intervals.
- The meters are sent to the HOKLAS accredited laboratory or equivalent to check and calibrated at yearly intervals.

3.6. Actions and Limit Level

The Action and Limit Levels were established in **Table 3.4** for noise monitoring.

Table 3.4 Action and Limit Levels for Noise Monitoring

<i>Time Period</i>	<i>Action</i>	<i>Limit</i>
0700 – 1900 hrs normal weekdays	When one documented complaint is received	75 dB(A)*

Remark: (*)70dB(A) for schools and 65dB(A) for schools during school examination period

3.7. Results and Observations

3.7.1. Results

Monitoring data of noise monitoring carried out in this reporting month are summarized in **Appendix E2**. Graphical presentation of noise monitoring results for the reporting month is shown in **Appendix E3**.

No exceedance of Action and Limit Level of noise monitoring results was recorded during the reporting month.

3.7.2. Observation

The noise monitoring data were found to be lower than the limit level. The major noise source during the monitoring event was the vehicles passing through the container yard entrance and the general earth works inside the construction site.

3.8 Event and Action Plan

If the impact monitoring results exceed the Action and Limit Levels, the actions specified in **Table 3.5** shall be carried out.

Table 3.5 Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level	<ol style="list-style-type: none"> 1. Notify IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC and Contractor; 4. Discuss with the Contractor and formulate remedial measures ; 5. Increase monitoring frequency to check the effectiveness of mitigation measures. 	<ol style="list-style-type: none"> 1. Review the analyzed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure mitigation measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposal to IEC; 2. Implement noise mitigation proposals.
Limit level	<ol style="list-style-type: none"> 1. Notify IEC, ER, EPD & Contractor; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD the causes 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure mitigation measures are properly implemented; 5. If exceedances continues, consider what portion of the work is 	<ol style="list-style-type: none"> 1. Undertake immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as

	<p>and actions taken for the exceedances;</p> <p>7. Assess the effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</p> <p>8. If exceedance stops, cease additional monitoring.</p>		<p>responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</p>	<p>determined by ER, until the exceedance is abated.</p>
--	---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------	--	-------------------------------------------------------------------------------------------------------------	----------------------------------------------------------

4. WATER QUALITY MONITORING

4.1. Monitoring Requirements

- 4.1.1. Water quality was monitored in the reporting month in accordance with the EM&A Manual at the one alternative water quality monitoring station, R1b (at Tin Shui Wai Nullah) which shown in **Figure 2**.

4.2 Monitoring Methodology and Equipment

For In-situ Water Quality Measurement

Dissolved Oxygen (DO) measuring equipment

A portable, weatherproof DO-measuring meter with built-in salinity compensation (e.g. YSI 85, YSI Pro 2030 or equivalent) was used in the baseline monitoring. It can be capable for measuring dissolved oxygen level in the range of 0-20 mg/L and 0-200 % saturation.

For Water Sampling and Sample Analysis

Water Sampler

A water sampler comprising a metal bucket was lowered into the water body.

Water Container

The sample container, made by high-density polythene, was rinsed with a portion of the water sample. The water sample was then transferred to the container, labelled with a unique sample ID and sealed with a screw cap. The water samples were stored in a cool box maintained at 4°C. The water samples will then be delivered to Environmental Laboratory of ETS-Testconsult Ltd (HOKLAS Registration No. 022) on the same day for analysis according to the Standard Method APHA 19ed.

The summary of testing methods of testing parameters required was shown in **Table 4.1**.

Table 4.1 Summary of Testing Procedures for water samples

<i>Parameters</i>	<i>Testing Procedure</i>	<i>Detection Limit</i>
<i>Turbidity</i>	<i>Dissolved Oxygen Meter Measurement</i>	<i>0.1 NTU</i>
<i>Dissolved Oxygen</i>	<i>In house method refer to APHA 19th ed 2130 B</i>	<i>0.01 mg/L</i>
<i>Total suspended solids</i>	<i>In house method refer to APHA 19th ed 2540D</i>	<i>0.1 mg/L</i>

4.3 Monitoring Frequency

- 4.3.1 Water samples were collected 3 times per week in 1 monitoring station. Three parameters including turbidity, dissolved oxygen and total suspended solids would be tested.

Table 4.2 Monitoring Frequency of Water Quality Monitoring

Parameters	Frequency	No. of sampling stations
Turbidity	3 times per week	1 station
Dissolved Oxygen		
Total suspended solids		

- 4.3.2 In this reporting period, a total of 14 occasions of water quality monitoring were undertaken and the schedule was shown in **Table 4.3**

Table 4.3 Time Schedule of Impact Water Quality Monitoring

June 2017						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
				1	2	3
4	5	6	7	8	9	10
11	12	13	14	15	16	17
18	19	20	21	22	23	24
25	26	27	28	29	30	

Remark: (▼) = Water quality monitoring carried out by ET.

4.4 Quality Assurance (QA) / Quality Control (QC)

For in-situ measurements, at each measurement / sampling, two consecutive measurements of turbidity and dissolved oxygen (DO) were taken. The probes were retrieved out of the water after the first measurement and then re-deployed for the second measurement. If the difference between the first and second measurement is greater than 25% the reading will be discarded and the measurements will be repeated.

For laboratory analysis of water, test method of all test parameters and the QA/QC samples were carried out in accordance with the requirements of HOKLAS.

For our QA/QC procedure, one QC sample, one duplicate sample and one sample spike of every batch of 20 samples were analyzed.

4.5 Actions and Limit Levels

The criteria for Action and Limit Levels have been set out as follows:

Table 4.4 The criteria of Action and Limit Levels for Water Quality

Parameters	Unit	Action Level	Limit Level
Turbidity	NTU	95%ile of baseline data	99%ile of baseline data
Dissolved Oxygen	mg/L	5%ile of baseline data	1%ile of baseline data
Suspended solids	mg/L	95%ile of baseline data	99%ile of baseline data

Following the criteria shown in **Table 4.4**, the Action and Limit Levels for monitoring parameters derived as illustrated in **Table 4.5**.

Table 4.5 Action and Limit Levels for Water Quality

<i>Parameters</i>	<i>Unit</i>	<i>Action</i>	<i>Limit</i>
<i>Turbidity</i>	<i>NTU</i>	<i>19.8</i>	<i>20.5</i>
<i>Dissolved Oxygen</i>	<i>mg/L</i>	<i>1.84</i>	<i>1.81</i>
<i>Suspended Solid</i>	<i>mg/L</i>	<i>17.0</i>	<i>17.8</i>

4.6 Result and Observation

4.6.1 Result

Monitoring data of water quality monitoring carried out in this reporting month are summarized in **Appendix F2**. Graphical presentation of the monitoring results for the reporting month is shown in **Appendix F3**.

According to the summary of water monitoring results, there was one limit level exceedance of suspended solid at station R1b on 13 June 2017. After investigation, there was concluded that the exceedance was not relevant to this Contract since there was no construction works conducted from 12:00noon on 12 June 2017 to 13:30pm on 13 June 2017 which was unlikely to generate suspended solid and thus deteriorate the water quality at the monitoring station R1b on 13 June 2017. Besides, Tropical Cyclone Warning Signal No.8 was hoisted from 12 to 13 June 2017 and Red Rainstorm Warning Signal was hoisted during water monitoring period on 13 June 2017 which would deteriorate the water quality at the monitoring station R1b on 13 June 2017. Indeed, a temporary storage pool was established in the lowest position of the construction site for acting as a prior sedimentation tank. The surface runoff was first stored in the temporary storage pool and then transferred to the Wetsep for proper treatment prior to discharge. The effluent was thus brought into an acceptable minimum level and also ensured to comply with the requirements specified in the discharge license. In addition, there was no water discharge in the morning of 13 June 2017. Thus, the exceedance of water samples taken from 11:38 to 11:49am on 13 June 2017 was considered as non-Project related. The Investigation Reports No. 001 (including the causes of exceedance, action taken and recommendation for mitigation) for Action or Limit Level Non-compliance were provided in **Appendix M**. Other than the above exceedance, no exceedance of Action and Limit level was recorded in the reporting month.

4.6.2 Observation

Generally, the turbidity and suspended solids were found to be lower than the action level. However, on 13 June 2017, the result of suspended solid was found to be extremely high comparing to the data recorded on other monitoring days. After investigation, it was most likely due to the above mentioned bad weather on 12 and 13 June 2017. Besides, all results of dissolved oxygen measured in this reporting month were higher than the action level.

4.7 Event and Action Plan

If the impact monitoring results of the individual parameters exceed the Action and Limit Levels, the actions specified in **Table 4.6** shall be carried out.

Table 4.6 Event and Action Plan for Water Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level being exceeded by one sampling day	1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on	1. Discuss with IEC on the proposed mitigation measures; 2. make agreement on	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify



Event	Action			
	ET Leader	IEC	ER	Contractor
	<p>compliance and sources of impact;</p> <p>3. Inform IEC and Contractor;</p> <p>4. Check monitoring data, all plant, equipment and Contractor's working methods;</p> <p>5. Discuss mitigation measures with IEC and Contractor;</p> <p>6. Repeat measurement on next day of exceedance.</p>	<p>mitigation measures submitted by Contractor and advise the ER accordingly;</p> <p>3. Assess the effectiveness of the implemented mitigation measures.</p>	<p>the mitigation measures to be implemented;</p> <p>3. Assess the effectiveness of the implemented mitigation measures.</p>	<p>unacceptable practice;</p> <p>3. Check all plant and equipment</p> <p>4. Consider changes of working methods;</p> <p>5. Discuss with ET and IEC and propose mitigation measures to IEC and ER;</p> <p>6. Implement the agreed mitigation measures.</p>
<p>Action Level being exceeded by more than two consecutive sampling days</p>	<p>1. Repeat in-situ measurement to confirm findings;</p> <p>2. Identify reasons for non-compliance and sources of impact;</p> <p>3. Inform IEC and Contractor;</p> <p>4. Check monitoring data, all plant, equipment and Contractor's working methods;</p> <p>5. Discuss mitigation measures with IEC and Contractor;</p> <p>6. Ensure mitigation measures are implemented;</p> <p>7. Prepare to increase the monitoring</p>	<p>1. Discuss with ET and Contractor on the mitigation measures;</p> <p>2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly;</p> <p>3. Assess the effectiveness of the implemented mitigation measures.</p>	<p>1. Discuss with IEC on the proposed mitigation measures;</p> <p>2. Make agreement on the mitigation measures to be implemented;</p> <p>3. Assess the effectiveness of the implemented mitigation measures.</p>	<p>1. Inform the ER and confirm notification of the non-compliance in writing;</p> <p>2. Rectify unacceptable practice;</p> <p>3. Check all plant and equipment;</p> <p>4. Consider changes of working methods;</p> <p>5. Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days;</p> <p>6. Implement the agreed mitigation measures.</p>



Event	Action			
	ET Leader	IEC	ER	Contractor
	8. frequency to daily; Repeat measurement on next day of exceedance.			
Limit Level being exceeded by one sampling day	1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures.

Event	Action			
	ET Leader	IEC	ER	Contractor
Limit Level being exceeded by more than two consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days. 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures; 5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit Level. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures; 7. As directed by the ER, to slow down or to stop all or part of the marine work or construction activities.

5. ENVIRONMENTAL SITE INSPECTION AND AUDIT

5.1. Site Inspection

- 5.1.1. Site Inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control mitigation measures for the project. During the reporting period, site inspections were carried out on 02, 09, 16, 23 & 30 June 2017.
- 5.1.2. Observations for the site inspections within this reporting period are summarized in **Table 5.1** and inspection checklists are attached in **Appendix H**.

Table 5.1 Summary of observation of site inspections

Date	Observations / Reminders	Follow-up Action	Closed Date
26 May 2017	<p>1. Stagnant pool in drip trays was observed. Follow-actions for outstanding observation will be inspected during the next site inspection.</p> <p>Reminder 1 – The contractor was reminded to provide temporary washing facilities with high pressure water jet before the completion of wheel washing bay.</p> <p>Reminder 2 – The contractor was reminded to provide seal between hoarding and the ground.</p>	1. Stagnant pool was cleared inside the drip trays.	02 June 2017
02 June 2017	<p>1. Stagnant pool was observed in the hole on the ground near sediment tank.</p> <p>2. Chemical container without label was observed.</p>	<p>1. Stagnant pool near sediment tank was cleared.</p> <p>2. Correct label was displayed on the chemical container.</p>	09 June 2017
09 June 2017	1. No items were observed.	--	--
16 June 2017	1. No items were observed.	--	--
23 June 2017	1. Oil Stain was observed on the ground at Portion P1.	1. Oil stains were cleaned.	30 June 2017
30 June 2017	1. Insufficient watering was observed	1. Follow-up actions for outstanding observation will be inspected during the next site inspection.	--

5.2. Advice on the Solid and Liquid Waste Management Status

5.2.1. All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil

5.2.2. The quantities of waste for disposal in this Reporting Period are summarized in **Table 5.2** and **Table 5.3** and the Monthly Summary Waste Flow Table is shown in **Appendix I**. Whenever possible, materials were reused on-site as far as practicable.

Table 5.2 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
Reused in this Contract (Inert) (m ³)	0	--
Reused in other Projects (Inert) (m ³)	0	--
Disposed as Public Fill (Inert) (m ³)	2,041	Tuen Mun 38 Fill Bank

Table 5.3 Summary of Quantities of C&D Materials

Type of Waste	Quantity	Disposal Location
Recycled Metal (kg)	0	--
Recycled Paper / Cardboard Packing (kg)	0	--
Recycled Plastic (kg)	0	--
Chemical Wastes (kg)	0	--
General Refuses (m ³)	12,300	North East New Territories (NENT) Landfill

- 5.2.3.** To control over the site performance on waste management, the Contractor shall ensure that all solid and liquid waste management works are in full compliance with the relevant license/permit requirements, such as the effluent discharge license and the chemical waste producer registration. The Contractor is also reminded to implement the recommended environmental mitigation measures according to the EM&A Manual based on actual site conditions.

5.3. Discharge License and Results of Effluent Monitoring

- 5.3.1.** Effluent quality was monitored in the reporting month in accordance with the EM&A Manual at the discharge point. A discharge license under Water Pollution Control Ordinance was obtained by the Contractor upon commencement of the Project. Self-monitoring would be performed as per the requirement under the discharge license. According to the EM&A Manual, pH, chemical oxygen demand and total suspended solid are required to be analysed at least once every two week.
- 5.3.2.** Effluent water samples were sampled by the Contractor on 10, 20 and 30 June 2017. The required testing parameter including pH, chemical oxygen demand and total suspended solid were carried out in a HOKLAS laboratory. The laboratory reports for the discharge water are presented in **Appendix N**.
- 5.3.3.** For effluent quality monitoring as per the discharge license requirement, the parameter complied with the discharge license requirement.

5.4. Environmental Licenses and Permits

- 5.4.1.** The valid environmental licenses and permits during the reporting period are summarized in **Appendix J**.

5.5. Implementation Status of Environmental Mitigation Measures

- 5.5.1.** The environmental mitigation measures that recommended in the Environmental Monitoring and Audit Manual covered the issues of dust, noise and waste and they are summarized as following:

Dust Mitigation Measures

- The working area for the uprooting of trees, shrubs, or vegetation or for the removal of boulders, poles, pillars or temporary or permanent structures should be sprayed with water or a dust suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;
- All demolished items (including trees, shrubs, vegetation, boulders, poles, pillars, structures, debris, rubbish and other items arising from site clearance) that may dislodge dust particles should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition;
- Vehicle washing facilities including a high pressure water jet should be provided at every discernible or designated vehicle exit point;
- The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;
- Where a site boundary adjoins a road, street, service and or other area accessible to the public, hoarding of not less than 2.4m from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit;

- f. Every main haul road (i.e. any course inside a construction site having a vehicle passing rate of higher than 4 in any 30 minutes) should be paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical so as to maintain the entire road surface wet;
- g. The portion of any road leading only to a construction site that is within 30m of a discernible or designated vehicle entrance or exit should be kept clear of dusty materials;
- h. Immediately before leaving a construction site, every vehicle should be washed to remove any dusty materials from its body and wheels;
- i. Where a vehicle leaving a construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle;
- j. The working area of any excavation or earth moving operation should be sprayed with water or a dusty suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;
- k. Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within 6 months after the last construction activity on the construction site or part of the construction site where the exposed earth lies;
- l. Any stockpile of dusty material should be either covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or a dust suppression chemical so as to maintain the entire surface wet.

Noise Mitigation Measures

- a. Quiet plants should be used in order to reduce the noise impacts to protect the nearby NSRs.
- b. Temporary and Movable Noise Barriers should be used in order to reduce the noise impact to the surrounding sensitive receivers
- c. The contractor should site noisy equipment and activities as far from sensitive receivers as practical.
- d. Idle equipment should be turned off or throttled down.
- e. Construction activities should be planned so that parallel operation of several sets of equipment close to a given receiver is avoided
- f. Construction plant should be properly maintained and operated.

Water Quality Mitigation Measures

- a. Exposed stockpiles should be covered with tarpaulin or impervious sheets before a rainstorm occurs;
- b. The exposed soil surfaces should also be properly protected to minimize dust emission;
- c. The stockpiles of materials should be placed in the locations away from the drainage channel so as to avoid releasing materials into the channel;
- d. Wheel washing facilities should be provided at site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles;
- e. Provision of site drainage systems and treatment facilities would be required to minimize the water pollution;
- f. A discharge license needs to be applied from EPD for discharging effluent from the construction site;
- g. The treated effluent quality is required to meet the requirements specified in the discharge license;
- h. Provision of chemical toilets is required to collect sewage from workforce. The chemical toilets should be cleaned on a regular basis;
- i. A licensed waste collector should be employed to clean the chemical toilets and temporary storage tank on a regular basis;
- j. Illegal disposal of chemicals should be strictly prohibited;
- k. Registration as a chemical waste producer is required if chemical wastes are generated and need to be disposed of. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes;
- l. Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance should be used as a guideline for handling chemical wastes;

- m. The impact from accidental spillage of chemicals can be effectively controlled through good management practices.

Waste Management Mitigation Measures

- a. Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;
- b. To encourage collection of aluminium cans by individual collectors, separate bins should be provided to segregate this waste from other general refuse generated by the workforce;
- c. Any unused chemicals or those with remaining functional capacity should be recycled;
- d. Prior to disposal of C&D waste, it is recommended that wood, steel and other metals be separated for re-use and/or recycling and inert waste as fill material to minimize the quantity of waste to be disposed of to landfill;
- e. Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and
- f. Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.

- 5.5.2. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in **Appendix K**. Most of the necessary mitigation measures were implemented properly. Any deficiencies were noted in the remarks of the schedule.

5.6. Summary of Exceedance of the Environmental Quality Performance Limit

- 5.6.1. There was no Action and Limit level exceedance of 1-hour and 24-hr TSP monitoring was recorded at station ASR1a and ASR2a during this reporting month.
- 5.6.2. There was no Action and Limit Level exceedance for noise recorded at station NSR1a and NSR2a during the reporting period.
- 5.6.3. According to the summary of water monitoring results, there was one limit level exceedance of suspended solid at station R1b on 13 June 2017. After investigation, there was concluded that the exceedance was not relevant to this Contract since there was no construction works conducted from 12:00noon on 12 June 2017 to 13:30pm on 13 June 2017 which was unlikely to generate suspended solid and thus deteriorate the water quality at the monitoring station R1b on 13 June 2017. Besides, Tropical Cyclone Warning Signal No.8 was hoisted from 12 to 13 June 2017 and Red Rainstorm Warning Signal was hoisted during water monitoring period on 13 June 2017 which would deteriorate the water quality at the monitoring station R1b on 13 June 2017. Indeed, a temporary storage pool was established in the lowest position of the construction site for acting as a prior sedimentation tank. The surface runoff was first stored in the temporary storage pool and then transferred to the Wetsep for proper treatment prior to discharge. The effluent was thus brought into an acceptable minimum level and also ensured to comply with the requirements specified in the discharge license. In addition, there was no water discharge in the morning of 13 June 2017. Thus, the exceedance of water samples taken from 11:38 to 11:49am on 13 June 2017 was considered as non-Project related. The Investigation Reports No. 001 (including the causes of exceedance, action taken and recommendation for mitigation) for Action or Limit Level Non-compliance were provided in **Appendix M**. Other than the above exceedance, no exceedance of Action and Limit level was recorded in the reporting month.

5.7. Summary of Complaints, Notification of Summons and Successful Prosecution

- 5.7.1. There were no complaints received during the reporting period.
- 5.7.2. There were no notifications of summons or prosecutions received during the reporting period.
- 5.7.3. A summary of environmental complaints, notifications of summons and successful prosecutions was given in **Table 5.4**.

Table 5.4 Summary of Environmental Complaints Notification of Summons and Successful Prosecution

Reporting Period	Cumulative Statistic		
	Complaints	Notifications of summons	Successful prosecutions
The reporting period	0	0	0
From commencement date of construction to end of reporting month	0	0	0

6. FUTURE KEY ISSUES

6.1 Construction Programme for the Coming Months

6.1.1 As informed by the Contractor, the major construction activities for July 2017 are included:

- *Piling Foundation (Prebored H-pile) for Chemically Enhanced Primary Treatment and Sludge Dewatering Building;*
- *Piling Foundation (Driven H-pile) for Inlet Work, Preliminary Treatment Works and Inlet Pumping Station;*
- *Piling Foundation (minipile);*
- *Portion 5 (Access Road) Works;*
- *Drainage Outlet connection (Effluent Connection to the Existing Junction Chamber);*
- *Diversion of Existing Street Lighting and Traffic Sign;*
- *Civil Works by ADCJV for HyD's Diversion of Existing Street Lighting and Traffic Signs;*
- *Civil Works by ADCJV for WSD's Diversion of Existing Watermains;*
- *Civil Works by ADCJV between Site Boundary for WSD's Diversion of Existing Watermains*

6.2 Key Issues for the Coming Month

Key issues to be considered in the coming month include:

- *Chemical and waste management;*
- *Treatment of runoff and wastewater prior to discharge; and*
- *Dust and Noise generated from construction activities;*

Mitigation measures to be required in the coming month:

Air Quality Impact

- To provide adequate water spraying in the worksite;
- To operate and maintain automatic wheel washing facilities properly;
- To provide road sweeping site entrance and public roads outside site entrance;
- To ensure implementation of the dust mitigation measures for the site activities;
- To maintain proper operation of the mist spraying system;
- To provide proper maintenance for vehicles and machines on site; and
- To investigate any other dust sources around the air sensitive receivers

Noise

- To switch off equipment if not in use;
- To operate silent equipment;
- To identify the noise sources inside and outside of the site; and
- To follow up any exceedance caused by the construction work inside the worksite

Water Quality Impact

- To ensure the drainage system was maintained properly;
- To maintain the existing silt trap to ensure good efficiency of wheel wash facilities;
- To avoid stagnant water in the drip trays due to rainfall;
- To avoid any stagnant water or provide insecticide to avoid mosquito breeding

Chemical and Waste Management

- To remove waste from the site regularly;
- To properly store and handle chemical wastes on site;
- To implement trip ticket system for all the imported public fill and general refuse disposal;
- To maintain proper housekeeping;
- To identify C&D material by packaging, labelling, storage, transportation and disposal in accordance with statutory regulations.

6.3 Environmental Monitoring and Site Inspection Schedule for the Coming Month

- 6.3.1** The tentative schedule for environmental monitoring and site inspection schedule for July 2017 is provided in **Appendix L**.


7. CONCLUSION**7.1 Conclusions**

- 7.1.1** There was no Action and Limit level exceedance of 1-hour and 24-hr TSP monitoring was recorded at station ASR1a and ASR2a during this reporting month.
- 7.1.2** There was no Action and Limit Level exceedance for noise recorded at station NSR1a and NSR2a during the reporting period.
- 7.1.3** According to the summary of water monitoring results, there was one limit level exceedance of suspended solid at station R1b on 13 June 2017. After investigation, there was concluded that the exceedance was not relevant to this Contract since there was no construction works conducted from 12:00noon on 12 June 2017 to 13:30pm on 13 June 2017 which was unlikely to generate suspended solid and thus deteriorate the water quality at the monitoring station R1b on 13 June 2017. Besides, Tropical Cyclone Warning Signal No.8 was hoisted from 12 to 13 June 2017 and Red Rainstorm Warning Signal was hoisted during water monitoring period on 13 June 2017 which would deteriorate the water quality at the monitoring station R1b on 13 June 2017. Indeed, a temporary storage pool was established in the lowest position of the construction site for acting as a prior sedimentation tank. The surface runoff was first stored in the temporary storage pool and then transferred to the Wetsep for proper treatment prior to discharge. The effluent was thus brought into an acceptable minimum level and also ensured to comply with the requirements specified in the discharge license. In addition, there was no water discharge in the morning of 13 June 2017. Thus, the exceedance of water samples taken from 11:38 to 11:49am on 13 June 2017 was considered as non-Project related. The Investigation Reports No. 001 (including the causes of exceedance, action taken and recommendation for mitigation) for Action or Limit Level Non-compliance were provided in **Appendix M**. Other than the above exceedance, no exceedance of Action and Limit level was recorded in the reporting month.
- 7.1.4** There were no complaints received during the reporting period.
- 7.1.5** There were no notifications of summons or prosecutions received during the reporting period.

- END OF REPORT -


Appendix A

Location of Works Areas

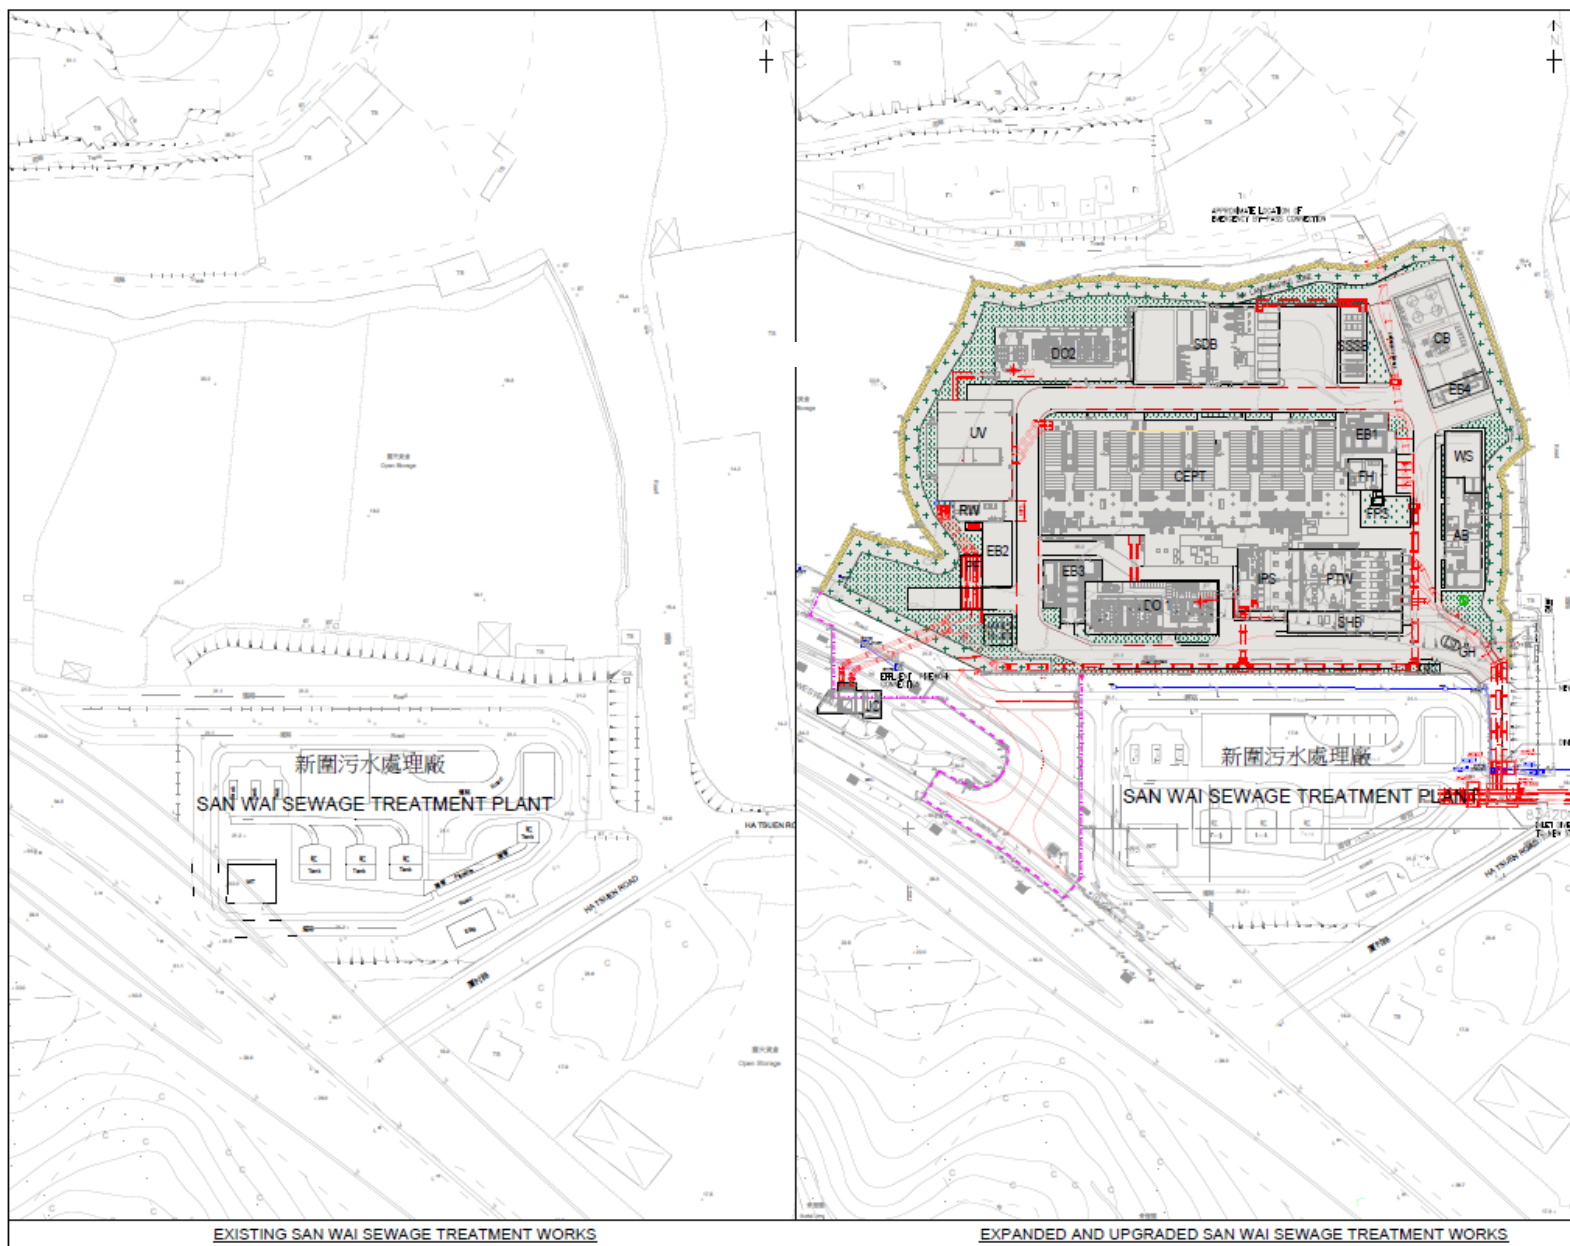

Appendix B

Project Organization Chart

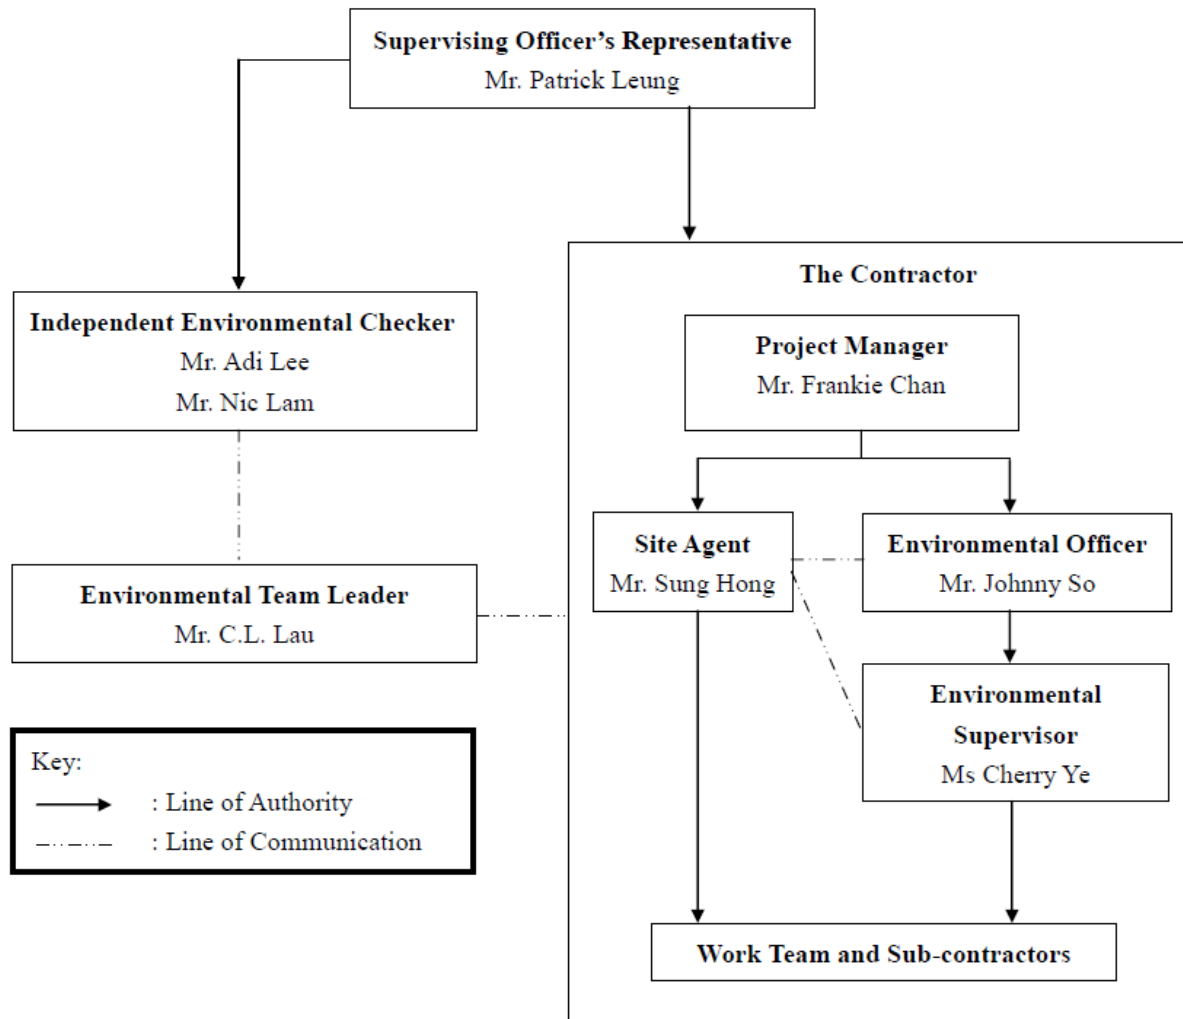

Appendix C

Construction Programme

DATA DATE: 30-Jun-17		LAYOUT: SW Project Phase 1 Rev 6 (3M 30Jun17)								PAGE 1 OF 6				
Activity ID	Activity Name	Original Duration	Start	Finish	Rev 6 BL Start	Rev 6 BL Finish	Slippage Start	Slippage Finish	Jun	Jul	2017 Aug	Sep	Oct	
San Wai Sewage Treatment Works Phase 1 - Rev 6 (Update as of 30 June 21														
Key Date														
Commencement & Completion of Works														
KD130	Section 1 - Period of Works (FOT P.3 cl 67.71) - Including 1.5 Days Granted EOT	552	27-May-16 A	29-Nov-17	27-May-16	29-Nov-17	0	0						
KD160	Section 2 - Period of Works (FOT P.3 cl 67.71) - Including 1.5 Days Granted EOT	1585	27-May-16 A	28-Sep-20	27-May-16	27-Sep-20	0	0						
Preliminaries & General Requirement														
Contractor Requirement														
PS465	Impact Monitoring	1204	27-Jun-17 A	25-Sep-20	09-Jun-17	24-Sep-20	-18	0						
PS475	Temporary Stockpile at DO2 Area	184	30-Jun-17	30-Dec-17	01-Jul-17	31-Dec-17	1	1						
PS485	Site Drainage Plan Implementation	1274	01-Apr-17 A	26-Sep-20	01-Apr-17	25-Sep-20	0	0						
Contractor Requirement for Working Area Portion (P1-P2)														
PS105	Fencing / Hoarding & Signboard Erection (P1,P2)	130	22-Nov-16 A	19-Jul-17	22-Nov-16	31-Mar-17	0	-110						
Site Establishment														
Site Establishment for Working Area Portion (P1-P2)														
PS322	Submission of CSD and CBWD 3D Model in LD3	150	30-Jun-17	26-Nov-17	01-Apr-17	28-Aug-17	-90	-90						
PS323	Submission of Clash Analysis Report	150	15-Jul-17	11-Dec-17	16-Apr-17	12-Sep-17	-90	-90						
Site Establishment for Working Area Portion (P8)														
PS390	TTMS for excavation of trial pits to ascertain the details of the existing rising mains - Submission to SO	0	30-Jun-17	30-Jun-17	31-May-17	31-May-17	-30	-30						
Design & Design Checking of Permanent Works														
Statutory Submission														
DS120	Designer Review Town Planning Submission	120	10-Oct-16 A	11-Jul-17	10-Oct-16	06-Feb-17	0	-155						
DS160	WSD - Water Supply & Plumbing	578	02-Feb-17 A	02-Sep-18	02-Feb-17	02-Sep-18	0	0						
DS165	CLP - Power Supply	751	01-Nov-16 A	22-Nov-18	01-Nov-16	21-Nov-18	0	0						
DS170	FSD - GBP with FS Notes and Dangerous Goods (DG)	283	02-Feb-17 A	11-Nov-17	02-Feb-17	11-Nov-17	0	0						
DS173	PCCW - Telephone Lines and Megalink	540	27-Jun-17 A	18-Dec-18	27-Jun-17	18-Dec-18	0	0						
DS174	PCCW - Telephone Lines for CLP Summation Metering	90	28-Jul-17 A	26-Sep-17	28-Jun-17	25-Sep-17	-30	0						
DS185	HAD - Home Affairs Department Application for Section 1 (ID KD150)	60	26-Jul-17	23-Sep-17	26-Jul-17	23-Sep-17	0	0						
DS205	Application for XP and TTMS for diverting traffic onto the Access Road in Portion P5 - Submission and Appr	290	30-Nov-16 A	16-Sep-17	30-Nov-16	15-Sep-17	0	0						
DS210	DLO - Submission and Approval of Tree Removal and Transplant Proposals	182	31-Jan-17 A	31-Jul-17	31-Jan-17	31-Jul-17	0	0						
DS230	GEO - Submission of DDA28A to SO for onward submission to GEO for Checking Certificate	283	11-May-17 A	10-Mar-18	11-May-17	17-Feb-18	0	-21						
DS236	EPD - Submission of Update EM&A to SO for onward submission to EPD for Approval	60	02-May-17 A	01-Jul-17	02-May-17	30-Jun-17	0	0						
DS238	EPD - Submission of Baseline Monitoring Report to SO for onward submission to EPD for Approval	60	19-May-17 A	10-Jul-17	12-May-17	10-Jul-17	-7	0						
Site Investigation														
DS380	Contamination Treatment (Biopile)	180	14-Jun-17 A	10-Dec-17	14-Jun-17	10-Dec-17	0	0						
AIP / DDA Submission & Approval														
DS410	Review & Revisions of Design Plan	340	26-Jun-16 A	30-Jun-17	26-Jun-16	31-May-17	0	-30						
Design Memorandum (AIP1 / DDA1)														
DS470	AIP1 - Design Memorandum - Design Preparation to SO Approval	186	26-Jun-16 A	01-Jul-17	26-Jun-16	28-Dec-16	0	-184						
Global Design														
Plant / Site Layout & Formation Level w/ GBP (AIP2 / DDA2)														
DG352	AIP2 - Plant / Site Layout Plan - Design Preparation to SO Approval	225	27-May-16 A	30-Jun-17	27-May-16	06-Jan-17	0	-175						
DG390	DDA2 - Plant / Site Layout Plan - Design Preparation to SO Approval	207	21-Oct-16 A	15-Jul-17	21-Oct-16	15-May-17	0	-61						
Treatment Process (AIP3 / DDA3)														
DG130	DDA3 - Treatment Process - Design Preparation to SO Approval	256	02-Sep-16 A	30-Jul-17	02-Sep-16	15-May-17	0	-76						
Hydraulic (AIP4 / DDA4)														
DG162	DDA4 - Hydraulic - Design Preparation to SO Approval	256	02-Sep-16 A	02-Aug-17	02-Sep-16	15-May-17	0	-79						
Alternative Permanent Access Road [Section 1] (AIP19 / DDA19)														

Remaining Level of Effort




Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone



TASK filter: 3 Months Rolling Programme.

CONTRACT NO. DC/2013/10 DESIGN, BUILD & OPERATE

SAN WAI SEWAGE TREATMENT - PHASE 1

MASTER SCHEDULE Rev 6 (30 June 2017)

THREE (3) MONTHS ROLLING PROGRAMME

Date	Revision	Ch...	Approved
30-Jun-17	Three (3) Months Rolling Programme		

DATA DATE: 30-Jun-17		LAYOUT: SW Project Phase 1 Rev 6 (3M 30Jun17)								PAGE 2 OF 6				
Activity ID	Activity Name	Original Duration	Start	Finish	Rev 6 BL Start	Rev 6 BL Finish	Slippage Start	Slippage Finish	2017	Jun	Jul	Aug	Sep	Oct
DG260	DDA19 - Access Road (Section 1) - Design Preparation to SO Approval	222	01-Oct-16 A	05-Jul-17	01-Oct-16	10-May-17	0	-56	DDA19 - Access Road (Section 1) - Design Preparation to SO Approval					
Electrical Power Supply System (AIP20 / DDA20ABCD)		347	27-Sep-16 A	09-Sep-17	27-Sep-16	08-Sep-17	0	0						
DG1879	AIP20 - Electrical Power Supply System - Design Preparation to SO Approval	185	27-Sep-16 A	29-Jul-17	27-Sep-16	30-Mar-17	0	-120	AIP20 - Electrical Power Supply System - Design Preparation to SO Approval					
DG1891	DDA20ABCD - Electrical Power Supply System - Design Preparation to SO Approval	246	24-Apr-17 A	09-Sep-17	06-Jan-17	08-Sep-17	-108	0	DDA20ABCD - Electrical Power Supply					
Control and Monitoring System (AIP21 / DDA21ABCDE)		469	09-Oct-16 A	04-Jan-18	09-Oct-16	04-Jan-18	0	0						
DG1905	AIP21 - Control & Monitoring System - Design Preparation to SO Approval	165	09-Oct-16 A	29-Jul-17	09-Oct-16	22-Mar-17	0	-128	AIP21 - Control & Monitoring System - Design Preparation to SO Approval					
DG1924	DDA21A - Process & Instrumentation Diagram (PID) - Design Preparation to SO Approval	286	12-Jan-17 A	25-Oct-17	12-Jan-17	24-Oct-17	0	0						
DG1940	DDA21B - System Control Philosophy - Design Preparation to SO Approval	219	20-Mar-17 A	25-Oct-17	20-Mar-17	24-Oct-17	0	0						
DG1956	DDA21C - Function Design Specification - Design Preparation to SO Approval	188	03-Apr-17 A	08-Nov-17	05-May-17	08-Nov-17	32	0						
DG1972	DDA21D - PLC, SCADA & I/O Allocation Schedules - Design Preparation to SO Approval	188	23-Apr-17 A	31-Oct-17	27-Apr-17	31-Oct-17	4	0						
DG1988	DDA21E - SCADA Graphic Interface - Design Preparation to SO Approval	188	01-Jul-17	04-Jan-18	01-Jul-17	04-Jan-18	0	0						
Landscaping Works (AIP22 / DDA22AB)		370	06-Jan-17 A	29-Dec-17	06-Jan-17	29-Dec-17	0	0						
DG1260	DDA22A - Landscaping Works (Green Roof) - Design Preparation to SO Approval	210	06-Jan-17 A	27-Aug-17	06-Jan-17	03-Aug-17	0	-24	DDA22A - Landscaping Works (Green Roof) - Design Preparation to SO Approval					
DG1274	DDA22B - Landscaping Works (Site Wide) - Design Preparation to SO Approval	180	03-Jul-17	29-Dec-17	03-Jul-17	29-Dec-17	0	0						
General Notes Drawings for Foundation and Civil & Structure (AIP24AB / DDA24AB)		213	21-Dec-16 A	27-Aug-17	21-Dec-16	21-Jul-17	0	-37						
General Notes Drawings for Civil & Structure (AIP24B / DDA24BC)		213	21-Dec-16 A	27-Aug-17	21-Dec-16	21-Jul-17	0	-37						
DG3690	DDA24B - Gen. Notes Dwg for Civil & Structure - Design Preparation to SO Approval	213	21-Dec-16 A	26-Aug-17	21-Dec-16	21-Jul-17	0	-35	DDA24B - Gen. Notes Dwg for Civil & Structure - Design Preparation to SO Approval					
DG3706	DDA24C - Typical Details for Architecture - Design Preparation to SO Approval	150	22-Feb-17 A	27-Aug-17	22-Feb-17	21-Jul-17	0	-37	DDA24C - Typical Details for Architecture - Design Preparation to SO Approval					
Geotechnical Report (AIP25 / DDA25A)		219	09-Oct-16 A	30-Jul-17	09-Oct-16	15-May-17	0	-76						
DG3445	DDA25A - Geotechnical Interpretation Report - Design Preparation to SO Approval	219	09-Oct-16 A	30-Jul-17	09-Oct-16	15-May-17	0	-76	DDA25A - Geotechnical Interpretation Report - Design Preparation to SO Approval					
Site Formation & Civil Works (AIP26 / DDA26)		218	14-Jan-17 A	18-Sep-17	14-Jan-17	19-Aug-17	0	-30						
DG660	DDA26 - Site Formation - Design Preparation to SO Approval	218	14-Jan-17 A	18-Sep-17	14-Jan-17	19-Aug-17	0	-30	DDA26 - Site Formation - Design Preparation to SO Approval					
Roadworks (AIP27A / DDA27A)		170	23-Mar-17 A	08-Sep-17	23-Mar-17	08-Sep-17	0	0						
DG1060	DDA27A - Roadworks - Design Preparation to SO Approval	170	23-Mar-17 A	08-Sep-17	23-Mar-17	08-Sep-17	0	0	DDA27A - Roadworks - Design Preparation to SO Approval					
Drainage Works (AIP27B / DDA27B)		170	21-Feb-17 A	08-Sep-17	21-Feb-17	09-Aug-17	0	-30						
DG960	DDA27B - Drainage - Design Preparation to SO Approval	170	21-Feb-17 A	08-Sep-17	21-Feb-17	09-Aug-17	0	-30	DDA27B - Drainage - Design Preparation to SO Approval					
Boundary Wall & Entrance (AIP28 / DDA28AB)		310	03-Feb-17 A	29-Dec-17	03-Feb-17	29-Dec-17	0	0						
DG1127	AIP28 - Slopes, Retaining Wall, Boundary Wall & Entrance - Design Preparation to SO Approval	118	03-Feb-17 A	27-Jul-17	03-Feb-17	31-May-17	0	-57	AIP28 - Slopes, Retaining Wall, Boundary Wall & Entrance - Design Preparation to SO Approval					
DG1160	DDA28A - Slopes and Retaining Wall - Design Preparation to SO Approval	167	03-Feb-17 A	14-Sep-17	03-Feb-17	19-Jul-17	0	-57	DDA28A - Slopes and Retaining Wall - Design Preparation to SO Approval					
DG1195	DDA28B - Boundary Wall & Entrance - Design Preparation to SO Approval	196	17-Jun-17 A	29-Dec-17	17-Jun-17	29-Dec-17	0	0						
Foundation & Piling Design (AIP29 / DDA29ABC)		154	16-Feb-17 A	12-Sep-17	16-Feb-17	19-Jul-17	0	-54						
DG495	DDA29B - Piling / Foundation - Design Preparation to SO Approval (Area 2)	112	16-Feb-17 A	29-Jul-17	16-Feb-17	07-Jun-17	0	-51	DDA29B - Piling / Foundation - Design Preparation to SO Approval (Area 2)					
DG510	DDA29C - Piling / Foundation - Design Preparation to SO Approval (Area 3)	112	30-Mar-17 A	12-Sep-17	30-Mar-17	19-Jul-17	0	-54	DDA29C - Piling / Foundation - Design Preparation to SO Approval (Area 3)					
Site Wide Utility (AIP30 / DDA30)		409	02-Oct-16 A	09-Dec-17	02-Oct-16	09-Dec-17	0	0						
DG3480	AIP30 - Site Wide Utility - Design Preparation to SO Approval	135	02-Oct-16 A	08-Jul-17	02-Oct-16	13-Feb-17	0	-144	AIP30 - Site Wide Utility - Design Preparation to SO Approval					
DG3515	DDA30A - Site Wide Security Access Control - Design Preparation to SO Approval	189	30-Jan-17 A	16-Sep-17	02-Feb-17	09-Aug-17	3	-37	DDA30A - Site Wide Security Access Control - Design Preparation to SO Approval					
DG3774	DDA30B - Underground Process Pipework - Design Preparation to SO Approval	170	08-Jun-17 A	24-Nov-17	08-Jun-17	24-Nov-17	0	0						
DG3788	DDA30C - Fire Services System and Street Fire Hydrant System - Design Preparation to SO Approval	170	08-Jun-17 A	24-Nov-17	08-Jun-17	24-Nov-17	0	0						
DG3802	DDA30D - Cable Route and Cable Draw Pit - Design Preparation to SO Approval	170	23-Jun-17 A	09-Dec-17	23-Jun-17	09-Dec-17	0	0						
DG3816	DDA30E - Misc. Small Electrical Power & Bldg. Services - Design Preparation to SO Approval	170	23-Jun-17 A	09-Dec-17	23-Jun-17	09-Dec-17	0	0						
DG3830	DDA30F - Typical Electrical Installation Drawings - Design Preparation to SO Approval	170	08-Jun-17 A	09-Dec-17	08-Jun-17	09-Dec-17	0	0						
DG3844	DDA30G - Typical Building Services Installation Drawings - Design Preparation to SO Approval	170	23-Jun-17 A	09-Dec-17	23-Jun-17	09-Dec-17	0	0						
DG3858	DDA30H - C&S Detailed Design Report for Pipe Trenches - Design Preparation to SO Approval	170	08-May-17 A	24-Oct-17	08-May-17	24-Oct-17	0	0						
HAZOP Report (DDA31AB)		366	01-Dec-16 A	28-Dec-17	01-Dec-16	28-Dec-17	0	0						
DG3530	DDA31A - HAZOP Study - Design Preparation to SO Approval	302	01-Dec-16 A	28-Sep-17	01-Dec-16	28-Sep-17	0	0	DDA31A - HAZOP Study - Design Preparation to SO Approval					
DG3545	DDA31B - Hazardous Zoning Classification Report - Design Preparation to SO Approval	119	31-Aug-17	28-Dec-17	01-Sep-17	28-Dec-17	0	0						
ELS / Bulk Excavation		215	22-Jan-17 A	09-Sep-17	22-Jan-17	24-Aug-17	0	-16						
DG3760	ELS / Bulk Excavation - Design Preparation to SO Approval	215	22-Jan-17 A	09-Sep-17	22-Jan-17	24-Aug-17	0	-16	ELS / Bulk Excavation - Design Preparation to SO Approval					
Miscellaneous Design		148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
Equipment Schedule (DDA32A)		148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
DG2012	DDA32A - Equipment Schedule - Design Preparation to SO Approval	148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
Penstock & Stoplogs Schedule (DDA32B)		148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
DG3216	DDA32B - Penstock & Stoplogs Schedule - Design Preparation to SO Approval	148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
Valves Schedule (DDA32C)		148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
DG3222	DDA32C - Valves Schedule - Design Preparation to SO Approval	148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
Piping Schedule (DDA32D)		148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						

DATA DATE: 30-Jun-17		LAYOUT: SW Project Phase 1 Rev 6 (3M 30Jun17)								PAGE 3 OF 6				
Activity ID	Activity Name	Original Duration	Start	Finish	Rev 6 BL Start	Rev 6 BL Finish	Slippage Start	Slippage Finish	Jun	Jul	2017 Aug	Sep	Oct	
DG3864	DDA32D - Piping Schedule - Design Preparation to SO Approval	148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
Painting Schedule (DDA32E)														
DG3228	DDA32E - Painting Schedule - Design Preparation to SO Approval	148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
Instrument and I/O Schedule (DDA32F)														
DG3234	DDA32F - Instrument and I/O Schedule - Design Preparation to SO Approval	148	03-Jul-17	27-Nov-17	03-Jul-17	27-Nov-17	0	0						
LOT #1 - Building / Facilities Design : CEPT+SF, PTW+IPS+SHB, UV, SDB+SSSB														
CEPT and System Control Flowmeter Chamber														
Civil and Structural Design (AIP6A / DDA6AB)														
DB1123	DDA6AB - CEPT & SF - C&S - Design Preparation to SO Approval	216	24-Dec-16	26-Aug-17	24-Dec-16	27-Jul-17	0	-29						
Electrical and Mechanical Design (AIP6B / DDA6C1C2DEF)														
DB1147	DDA6C1-1 - CEPT & SF - E&M (Piling & Foundation Design) - Design Preparation to SO Approval	435	27-May-16	29-Jan-18	31-Aug-16	08-Feb-18	96	11						
DB1160	DDA6C1-2 - CEPT & SF - E&M (Super Structural Design) - Design Preparation to SO Approval	273	31-Aug-16	11-Jul-17	31-Aug-16	30-May-17	0	-42						
DB1174	DDA6C2-1 - CEPT & SF - E&M (Piling & Foundation Design) - Design Preparation to SO Approval	185	28-Jul-17	29-Jan-18	08-Aug-17	08-Feb-18	11	11						
DB1188	DDA6C2-2 - CEPT & SF - E&M (Super Structural Design) - Design Preparation to SO Approval	273	27-May-16	16-Jul-17	31-Aug-16	30-May-17	96	-47						
DB4508	DDA6DEF - CEPT & System Control - E&M - Design Preparation to SO Approval	289	28-Jan-17	10-Nov-17	25-Jan-17	09-Nov-17	0	0						
Inlet Work, Preliminary Treatment Works, IPS and SHB														
Civil and Structural Design (AIP5A / DDA5AB1B2)														
DB1223	DDA5A - PTW, IPS & SHB - C&S - Design Preparation to SO Approval	236	26-Nov-16	05-Sep-17	26-Nov-16	19-Jul-17	0	-47						
DB4814	DDA5B1 - PTW & IPS - C&S - Design Preparation to SO Approval	215	17-Dec-16	31-Aug-17	17-Dec-16	19-Jul-17	0	-43						
DB4830	DDA5B2 - SHB - C&S - Design Preparation to SO Approval	215	06-Feb-17	08-Sep-17	06-Feb-17	08-Sep-17	0	0						
Electrical and Mechanical Design (AIP5B / DDA5C1C2DEF)														
DB1249	DDA5C1-1 - PTW, IPS & SHB - E&M (Piling & Foundation Design) - Design Preparation to SO Approval	349	27-May-16	14-Sep-17	10-Sep-16	09-Aug-17	106	-35						
DB1264	DDA5C1-2 - PTW, IPS & SHB - E&M (Super Structural Design) - Design Preparation to SO Approval	245	27-May-16	05-Jul-17	10-Sep-16	12-May-17	106	-54						
DB1280	DDA5C2-1 - PTW, IPS & SHB - E&M (Piling & Foundation Design) - Design Preparation to SO Approval	131	01-Apr-17	14-Sep-17	01-Apr-17	09-Aug-17	0	-35						
DB1296	DDA5C2-2 - PTW, IPS & SHB - E&M (Super Structural Design) - Design Preparation to SO Approval	245	10-Sep-16	05-Jul-17	10-Sep-16	12-May-17	0	-54						
DB4524	DDA5DEF - PTW, IPS & SHB - E&M - Design Preparation to SO Approval	131	01-Mar-17	14-Sep-17	01-Apr-17	09-Aug-17	31	-35						
UV Disinfection Facilities														
Civil and Structural Design (AIP7A / DDA7AB)														
DB1325	DDA7AB - UV Facilities - C&S - Design Preparation to SO Approval	208	27-Nov-16	24-Aug-17	27-Nov-16	22-Jun-17	0	-63						
Electrical and Mechanical Design (AIP7B / DDA7C1C2DEF)														
DB1382	DDA7C1-1 - UV Facilities - E&M (Piling & Foundation Design) - Design Preparation to SO Approval	481	22-Dec-16	09-May-18	22-Dec-16	09-May-18	0	0						
DB1368	DDA7C1-2 - UV Facilities - E&M (Super Structural Design) - Design Preparation to SO Approval	261	22-Dec-16	08-Sep-17	22-Dec-16	08-Sep-17	0	0						
DB1384	DDA7C2-1 - UV Facilities - E&M (Piling & Foundation Design) - Design Preparation to SO Approval	243	08-Sep-17	09-May-18	09-Sep-17	09-May-18	0	0						
DB1399	DDA7C2-2 - UV Facilities - E&M (Super Structural Design) - Design Preparation to SO Approval	261	22-Dec-16	08-Sep-17	22-Dec-16	08-Sep-17	0	0						
DB4540	DDA7DEF - UV Facilities - E&M - Design Preparation to SO Approval	253	30-Jun-17	10-Mar-18	01-Jul-17	10-Mar-18	0	0						
Sludge Dewatering Building and Sludge Skip Storage Building														
Civil and Structural Design (AIP8A / DDA8AB1B2)														
DB1433	DDA8A - SDB and SSSB - C&S - Design Preparation to SO Approval	470	25-Sep-16	09-Sep-17	25-Sep-16	08-Sep-17	0	0						
DB4844	DDA8B1 - SDB - C&S - Design Preparation to SO Approval	217	24-Dec-16	13-Sep-17	24-Dec-16	28-Jul-17	0	-46						
DB4858	DDA8B2 - SSSB - C&S - Design Preparation to SO Approval	175	04-Feb-17	13-Sep-17	04-Feb-17	28-Jul-17	0	-46						
Electrical and Mechanical Design (AIP8B / DDA8C1C2DEF)														
DB1460	DDA8C1-1 - SDB and SSSB - E&M (Piling & Foundation Design) - Design Preparation to SO Approval	470	25-Sep-16	09-Sep-17	25-Sep-16	08-Sep-17	0	0						
DB1476	DDA8C1-2 - SDB and SSSB - E&M (Super Structural Design) - Design Preparation to SO Approval	227	25-Sep-16	16-Aug-17	25-Sep-16	09-May-17	0	-99						
DB1492	DDA8C2-1 - SDB and SSSB - E&M (Piling & Foundation Design) - Design Preparation to SO Approval	133	29-Apr-17	09-Sep-17	29-Apr-17	08-Sep-17	0	0						
DB1508	DDA8C2-2 - SDB and SSSB - E&M (Super Structural Design) - Design Preparation to SO Approval	227	25-Sep-16	16-Aug-17	25-Sep-16	09-May-17	0	-99						
DB4556	DDA8DEF - SDB and SSSB - E&M - Design Preparation to SO Approval	133	29-Apr-17	09-Sep-17	29-Apr-17	08-Sep-17	0	0						
LOT #2 - Building / Facilities Design : AB+WS, DO, CB+EB4, FH														
Chemical Building and EB 4														
Civil and Structural Design for CB & EB4 (AIP12A / DDA12AB)														
DB2123	DDA12AB - Chemical Building & EB4 - C&S - Design Preparation to SO Approval	376	28-Sep-16	08-Oct-17	28-Sep-16	08-Oct-17	0	0						
Electrical and Mechanical Design for CB only (AIP12B / DDA12C1C2DEF)														
DB2148	DDA12C1C2 - Chemical Building - E&M - Design Preparation to SO Approval	247	28-Sep-16	29-Jul-17	28-Sep-16	01-Jun-17	0	-58						
DB4602	DDA12DEF - Chemical Building - E&M - Design Preparation to SO Approval	246	05-Feb-17	08-Oct-17	05-Feb-17	08-Oct-17	0	0						
Administration Building & Maintenance Workshop														
Civil and Structural Design (AIP10A / DDA10AB)														
DB2234	DDA10AB - Admin Bldg. & Workshop - C&S - Design Preparation to SO Approval	426	01-Sep-16	13-Sep-17	01-Sep-16	08-Sep-17	0	-5						
Electrical and Mechanical Design (AIP10B / DDA10C1C2DEF)														
DB2234	DDA10AB - Admin Bldg. & Workshop - C&S - Design Preparation to SO Approval	186	22-Jan-17	13-Sep-17	22-Jan-17	26-Jul-17	0	-49						
DB2234	DDA10AB - Admin Bldg. & Workshop - C&S - Design Preparation to SO Approval	186	22-Jan-17	13-Sep-17	22-Jan-17	26-Jul-17	0	-49						


DATA DATE: 30-Jun-17		LAYOUT: SW Project PHase 1 Rev 6 (3M 30Jun17)								PAGE 4 OF 6				
Activity ID	Activity Name	Original Duration	Start	Finish	Rev 6 BL Start	Rev 6 BL Finish	Slippage Start	Slippage Finish	2017	Jun	Jul	Aug	Sep	Oct
DB2273	AIP10B - Admin Bldg. & Workshop - E&M - Design Preparation to SO Approval	190	01-Sep-16	30-Jul-17	01-Sep-16	09-Mar-17	0	-143						
DB2286	DDA10C1C2 - Admin Bldg. & Workshop - E&M - Design Preparation to SO Approval	295	03-Oct-16	24-Aug-17	03-Oct-16	24-Jul-17	0	-31						
DB4618	DDA10DEF - Admin Bldg. & Workshop - E&M - Design Preparation to SO Approval	221	31-Jan-17	08-Sep-17	31-Jan-17	08-Sep-17	0	0						
Deodorization Facilities No.1 and No.2														
Civil and Structural Design (AIP9A / DDA9AB)														
DB2323	DDA9AB - DO #1 & #2 - C&S - Design Preparation to SO Approval	206	26-Jan-17	19-Sep-17	26-Jan-17	19-Aug-17	0	-30						
Electrical and Mechanical Design (AIP9B / DDA9C1C2DEF)														
DB2348	DDA9C1C2 - DO #1 & #2 - E&M - Design Preparation to SO Approval	146	15-Dec-16	13-Aug-17	15-Dec-16	09-May-17	0	-96						
DB4634	DDA9DEF - DO #1 & #2 - E&M - Design Preparation to SO Approval	256	26-Jan-17	09-Oct-17	26-Jan-17	08-Oct-17	0	0						
Street Fire Hydrant Pump Room & GENSET Room														
Civil and Structural Design (AIP17A / DDA17AB)														
DB2423	DDA17AB - FH Pump Room & GENSET Room - C&S - Design Preparation to SO Approval	232	23-Mar-17	10-Nov-17	23-Mar-17	09-Nov-17	0	0						
Electrical and Mechanical Design (AIP17B / DDA17C1C2DE)														
DB2448	DDA17C1C2 - FH Pump Room & GENSET Room - E&M - Design Preparation to SO Approval	213	07-Dec-16	24-Aug-17	07-Dec-16	07-Jul-17	0	-48						
DB4648	DDA17DE - FH Pump Room & GENSET Room - E&M - Design Preparation to SO Approval	262	23-Mar-17	10-Dec-17	23-Mar-17	09-Dec-17	0	0						
LOT #3 - Building / Facilities Design : EB1, EB2, EB3, EB4, RW, DG+ICW, Inlet/Outlet														
Electrical Building No.1, No.2, No.3, No.4														
Civil and Structural Design for EB123 (AIP13A / DDA13AB)														
DB3123	DDA13AB - EB1, EB2 and EB3 - C&S - Design Preparation to SO Approval	147	08-Apr-17	01-Sep-17	08-Apr-17	01-Sep-17	0	0						
Electrical and Mechanical Design for EB1234 (AIP13B / DDA13C1C2DE)														
DB3148	DDA13C1C2 - EB1, EB2, EB3 & EB4 - E&M - Design Preparation to SO Approval	246	16-Sep-16	16-Aug-17	21-Sep-16	24-May-17	5	-84						
DB4664	DDA13DE - EB1, EB2, EB3 & EB4 - E&M - Design Preparation to SO Approval	191	23-Feb-17	16-Sep-17	23-Feb-17	01-Sep-17	0	-15						
Re-use Water Building														
Civil and Structural Design (AIP14A / DDA14AB)														
DB3223	DDA14AB - Re-use water Building - C&S - Design Preparation to SO Approval	166	13-Apr-17	25-Sep-17	13-Apr-17	25-Sep-17	0	0						
Electrical and Mechanical Design (AIP14B / DDA14C1C2DEF)														
DB3248	DDA14C1C2 - Re-use water Building - E&M - Design Preparation to SO Approval	351	03-Dec-16	18-Nov-17	03-Dec-16	18-Nov-17	0	0						
DB4680	DDA14DEF - Re-use water Building - E&M - Design Preparation to SO Approval	220	13-Apr-17	18-Nov-17	13-Apr-17	18-Nov-17	0	0						
ICW and DG Store & Chemical Waste Storage Building														
Civil and Structural Design (AIP16A / DDA16AB)														
DB3323	DDA16AB - ICW, DG & Chemical Stores - C&S - Design Preparation to SO Approval	173	11-Mar-17	01-Sep-17	11-Mar-17	02-Aug-17	0	-30						
Electrical and Mechanical Design (AIP16B / DDA16C1C2DE)														
DB3348	DDA16C1C2 - ICW, DG & Chemical Stores - E&M - Design Preparation to SO Approval	245	30-Nov-16	24-Aug-17	30-Nov-16	01-Aug-17	0	-23						
DB4694	DDA16DE - ICW, DG & Chemical Stores - E&M - Design Preparation to SO Approval	199	24-May-17	09-Dec-17	24-May-17	08-Dec-17	0	0						
Inlet & Outlet Pipe Connections and Diversion Pipeworks														
Civil and Structural Design (AIP11 / DDA11)														
DB3424	DDA11A - C&S Detailed Design Report for Outlet Pipe Connection - Design Preparation to SO Approval	130	29-Nov-16	13-Aug-17	29-Nov-16	07-Apr-17	0	-128						
DB3438	DDA11B - C&S Detailed Design Report for Inlet Pipe Connection - Design Preparation to SO Approval	140	08-Apr-17	11-Sep-17	08-Apr-17	25-Aug-17	0	-16						
DB3452	DDA11C - C&S Detailed Design Report for Emergency Bypass - Design Preparation to SO Approval	140	31-Dec-16	29-Aug-17	28-Feb-17	17-Jul-17	59	-42						
LOT #4 - Building / Facilities Design : GH, PF														
Payment Flowmeter Chamber														
Civil and Structural Design (AIP15A / DDA15AB)														
DB4323	DDA15AB - Payment Flowmeter - C&S - Design Preparation to SO Approval	119	13-Apr-17	08-Sep-17	13-Apr-17	09-Aug-17	0	-30						
Electrical and Mechanical Design (AIP15B / DDA15C1C2DEF)														
DB4348	DDA15C1C2 - Payment Flowmeter - E&M - Design Preparation to SO Approval	309	25-Nov-16	26-Dec-17	03-Dec-16	25-Dec-17	8	0						
DB4740	DDA15DEF - Payment Flowmeter - E&M - Design Preparation to SO Approval	249	25-Nov-16	27-Aug-17	03-Dec-16	08-Aug-17	8	-19						
Gatehouse														
Civil and Structural Design (AIP18A / DDA18AB)														
DB4424	DDA18AB - Gatehouse - C&S - Design Preparation to SO Approval	160	18-Jul-17	24-Dec-17	18-Jul-17	24-Dec-17	0	0						
Electrical and Mechanical Design (AIP18B / DDA18C)														
DB4473	AIP18B - Gatehouse - E&M - Design Preparation to SO Approval	330	14-Jan-17	09-Dec-17	14-Jan-17	09-Dec-17	0	0						
DB4754	DDA18C - Gatehouse - E&M - Design Preparation to SO Approval	125	14-Jan-17	05-Jul-17	14-Jan-17	18-May-17	0	-48						
Civil & Structural Works														
LOT #1 - Bldg / Facilities Const. (Arch'l & Struct'l) : CEPT+SF, PTW+IPS+SHB, UV, SD														
Chemically Enhanced Primary Treatment (CEPT)														
CS1500	Piling Foundation (Prebored H-pile) 177 (D1, D2, E1, E2) + Trial Pile	89	17-May-17	13-Aug-17	17-May-17	13-Aug-17	0	0						

DATA DATE: 30-Jun-17			LAYOUT: SW Project Phase 1 Rev 6 (3M 30Jun17)								PAGE 5 OF 6				
Activity ID	Activity Name	Original Duration	Start	Finish	Rev 6 BL Start	Rev 6 BL Finish	Slippage Start	Slippage Finish	2017						
									Jun	Jul	Aug	Sep	Oct		
CS1505	Pile Loading Test	30	13-Aug-17	12-Sep-17	14-Aug-17	12-Sep-17	0	0					Pile Loading Test		
CS1507	Post-Drilling	30	13-Aug-17	12-Sep-17	14-Aug-17	12-Sep-17	0	0					Post-Drilling		
CS1510	Substructure (ELS & Bulk excavation)	70	12-Sep-17	21-Nov-17	13-Sep-17	21-Nov-17	0	0							
Inlet Work, Preliminary Treatment Works and Inlet Pumping Station (PTW & IPS)			182	30-May-17 A	21-Oct-17	30-May-17	21-Oct-17	0	0						
CS1200	Piling Foundation (Driven H-pile) 96 #2-1 (B1) + Trial Pile	80	30-May-17 A	17-Aug-17	30-May-17	17-Aug-17	0	0					Piling Foundation (Driven H-pile) 96 #2-1 (B1) + Trial Pile		
CS1205	Pile Loading Test	20	18-Aug-17	06-Sep-17	18-Aug-17	06-Sep-17	0	0					Pile Loading Test		
CS1207	Post-Drilling	20	18-Aug-17	06-Sep-17	18-Aug-17	06-Sep-17	0	0					Post-Drilling		
CS1210	Substructure (ELS & Bulk excavation)	45	07-Sep-17	21-Oct-17	07-Sep-17	21-Oct-17	0	0					Subst		
Solid Handling Building (SHB)			68	09-Sep-17	15-Nov-17	09-Sep-17	15-Nov-17	0	0						
CS1300	Substructure (rc structure)	68	09-Sep-17	15-Nov-17	09-Sep-17	15-Nov-17	0	0							
UV Disinfection Facility (UV)			80	12-Sep-17	01-Dec-17	20-Jul-17	07-Oct-17	-54	-54						
CS1900	Piling Foundation (minipile) 75 #3-1 (C1)	80	12-Sep-17	01-Dec-17	20-Jul-17	07-Oct-17	-54	-54							
Sludge Dewatering Building (SDB)			90	29-Jul-17	27-Oct-17	30-Jun-17	27-Sep-17	-29	-29						
CS1800	Piling Foundation (Prebored H-pile) 66 (E3)	90	29-Jul-17	27-Oct-17	30-Jun-17	27-Sep-17	-29	-29							
CS1810	Piling Foundation (minipile) 10 #1-1 (A1) + Trial Pile	60	29-Jul-17	27-Sep-17	30-Jun-17	28-Aug-17	-29	-29					Piling Foundation (minipile)		
Sludge Skip Storage Building (SSSB)			82	13-Sep-17	04-Dec-17	29-Jul-17	18-Oct-17	-46	-46						
CS2900	Substructure (rc structure)	82	13-Sep-17	04-Dec-17	29-Jul-17	18-Oct-17	-46	-46							
LOT #2 - Bldg / Facilities Const. (Arch'l & Struct'l) : AB+WS, DO, CB, FH			95	08-Sep-17	12-Dec-17	27-Jul-17	11-Nov-17	-43	-30						
Administration Building & Maintenance Workshop (AB & WS)			50	13-Sep-17	02-Nov-17	27-Jul-17	14-Sep-17	-49	-49						
CS1110	Substructure (rc structure)	50	13-Sep-17	02-Nov-17	27-Jul-17	14-Sep-17	-49	-49							
Deodorization Facilities No. 1 (DO 1)			84	19-Sep-17	12-Dec-17	20-Aug-17	11-Nov-17	-30	-30						
CS1610	Substructure (rc structure)	84	19-Sep-17	12-Dec-17	20-Aug-17	11-Nov-17	-30	-30							
Chemical Building (CB)			91	08-Sep-17	07-Dec-17	08-Aug-17	06-Nov-17	-31	-31						
CS2310	Substructure (rc structure)	91	08-Sep-17	07-Dec-17	08-Aug-17	06-Nov-17	-31	-31							
LOT #3 - Bldg / Facilities Const. (Arch'l & Struct'l) : EB, RW, DG, ICW, JC			136	02-Sep-17	15-Jan-18	03-Aug-17	15-Jan-18	-30	0						
Electrical Building No.1 (EB1) CEPT			136	02-Sep-17	15-Jan-18	02-Sep-17	15-Jan-18	0	0						
CS2410	Substructure (rc structure)	136	02-Sep-17	15-Jan-18	02-Sep-17	15-Jan-18	0	0							
Electrical Building No.4 (EB4) CB			85	08-Sep-17	01-Dec-17	08-Aug-17	31-Oct-17	-31	-31						
CS2710	Substructure (rc structure)	85	08-Sep-17	01-Dec-17	08-Aug-17	31-Oct-17	-31	-31							
Re-use Water Building (RW)			62	26-Sep-17	26-Nov-17	26-Sep-17	26-Nov-17	0	0						
CS2010	Substructure (rc structure)	62	26-Sep-17	26-Nov-17	26-Sep-17	26-Nov-17	0	0							
DG Store and Chemical Waste Storage Building (DG)			75	02-Sep-17	15-Nov-17	03-Aug-17	16-Oct-17	-30	-30						
CS2800	Substructure (rc structure)	75	02-Sep-17	15-Nov-17	03-Aug-17	16-Oct-17	-30	-30							
Irrigation & Cleansing Water Pump Room (ICW)			75	02-Sep-17	15-Nov-17	03-Aug-17	16-Oct-17	-30	-30						
CS3370	Substructure (rc structure)	75	02-Sep-17	15-Nov-17	03-Aug-17	16-Oct-17	-30	-30							
Existing Junction Chamber (JC)			50	10-Sep-17	29-Oct-17	25-Aug-17	13-Oct-17	-16	-16						
CS2190	Substructure (ELS & Bulk excavation)	50	10-Sep-17	29-Oct-17	25-Aug-17	13-Oct-17	-16	-16							
External Works & Miscellaneous			280	08-Apr-17 A	13-Mar-18	08-Apr-17	28-Feb-18	0	-13						
CS3203	Slope works (Northern Portion)	180	15-Sep-17	13-Mar-18	20-Jul-17	15-Jan-18	-57	-57							
CS3220	Drainage Outlet connection (Effluent Connection to the Existing Junction Chamber)	210	08-Apr-17 A	04-Nov-17	08-Apr-17	03-Nov-17	0	0							
CS3240	Portion 5 (Access Road) Works	201	12-May-17 A	28-Oct-17	12-May-17	28-Nov-17	0	31							
CS3282	Diversion of Existing Street Lighting and Traffic Signs (P5)	61	01-Jun-17 A	31-Jul-17	01-Jun-17	31-Jul-17	0	0					Diversion of Existing Street Lighting and Traffic Signs (P5)		
CS3283	Civil Works by ADC JV for HyD's Diversion of Existing Street Lighting and Traffic Signs (P5)	61	01-Jun-17 A	31-Jul-17	01-Jun-17	31-Jul-17	0	0					Civil Works by ADC JV for HyD's Diversion of Existing Street Lighting and Traffic Signs (P5)		
CS3286	Civil Works by ADC JV for WSD's Diversion of Existing Watermains	106	01-Jun-17 A	14-Sep-17	01-Jun-17	14-Sep-17	0	0					Civil Works by ADC JV for WSD's Diversion of Existing Watermains		
CS3288	Civil Works by ADC JV between Site Boundary for WSD's Diversion of Existing Watermains	273	01-Jun-17 A	14-Jan-18	01-Jun-17	28-Feb-18	0	46					Civil Works by ADC JV for WSD's Diversion of Existing Watermains		
E&M Works			664	15-Jul-16 A	22-Feb-19	15-Jul-16	26-Jan-19	0	-27						
Procurement			664	15-Jul-16 A	22-Feb-19	15-Jul-16	26-Jan-19	0	-27						
Administration Building & Maintenance Workshop (AB & WS)			455	12-Dec-16 A	28-Jul-18	12-Dec-16	28-Jul-18	0	0						
EM3125	Inquiry & Purchase Orders	360	12-Dec-16 A	06-Dec-17	12-Dec-16	06-Dec-17	0	0							
EM3130	Manufacturing & Logistic	369	25-Jul-17	28-Jul-18	25-Jul-17	28-Jul-18	0	0							
Inlet Work, Preliminary Treatment Units and Inlet Pumping Station (PTW & IPS)			586	04-Jan-17 A	22-Feb-19	04-Jan-17	26-Jan-19	0	-27						
EM3135	Inquiry & Purchase Orders	480	04-Jan-17 A	28-Apr-18	04-Jan-17	28-Apr-18	0	0							
EM3140	Manufacturing & Logistic	580	23-Jul-17	22-Feb-19	26-Jun-17	26-Jan-19	-27	-27							
Solid Handling Building (SHB)			450	12-Apr-17 A	15-Sep-18	12-Apr-17	19-Aug-18	0	-27						

DATA DATE: 30-Jun-17		LAYOUT: SW Project Phase 1 Rev 6 (3M 30Jun17)								PAGE 6 OF 6				
Activity ID	Activity Name	Original Duration	Start	Finish	Rev 6 BL Start	Rev 6 BL Finish	Slippage Start	Slippage Finish	Jun	Jul	2017 Aug	Sep	Oct	
EM3145	Inquiry & Purchase Orders	320	12-Apr-17	25-Feb-18	12-Apr-17	25-Feb-18	0	0						
EM3150	Manufacturing & Logistic	420	23-Jul-17	15-Sep-18	26-Jun-17	19-Aug-18	-27	-27						
System Control Flowmeter Chamber (SF)														
EM3155	Inquiry & Purchase Orders	404	17-Aug-16	08-Jun-18	17-Aug-16	07-Jun-18	0	0						
EM3160	Manufacturing & Logistic	379	17-Aug-16	31-Aug-17	17-Aug-16	30-Aug-17	0	0						
Chemically Enhanced Primary Treatment (CEPT)														
EM3115	Inquiry & Purchase Orders	499	26-Aug-16	10-Sep-18	26-Aug-16	10-Sep-18	0	0						
EM3120	Manufacturing & Logistic	401	26-Aug-16	30-Sep-17	26-Aug-16	30-Sep-17	0	0						
Deodorization Facilities No. 1 & 2 (DO 1 & DO 2)														
EM3165	Inquiry & Purchase Orders	480	10-Jan-17	04-May-18	10-Jan-17	04-May-18	0	0						
Street Fire Hydrant Pump Room & GENSET Room (FH)														
EM3275	Inquiry & Purchase Orders	230	18-Jan-17	10-Dec-17	24-Apr-17	09-Dec-17	96	0						
Gatehouse (GH)														
EM3285	Inquiry & Purchase Orders	247	07-Apr-17	09-Dec-17	07-Apr-17	09-Dec-17	0	0						
SCADA and CMMS Systems														
EM3330	Inquiry & Purchase Orders	295	06-Jan-17	28-Oct-17	06-Jan-17	27-Oct-17	0	0						
Sludge Dewatering Building (SDB)														
EM3175	Inquiry & Purchase Orders	560	04-Nov-16	17-May-18	04-Nov-16	17-May-18	0	0						
Payment Flowmeter Chamber (PF)														
EM3205	Inquiry & Purchase Orders	379	17-Aug-16	31-Aug-17	17-Aug-16	30-Aug-17	0	0						
EM3210	Manufacturing & Logistic	333	10-Jul-17	08-Jun-18	10-Jul-17	07-Jun-18	0	0						
Existing Junction Chamber (JC)														
EM3215	Inquiry & Purchase Orders	236	07-Jan-17	01-Jan-18	07-Jan-17	01-Jan-18	0	0						
EM3220	Manufacturing & Logistic	180	07-Jan-17	05-Jul-17	07-Jan-17	05-Jul-17	0	0						
Chemical Building (CB)														
EM3225	Inquiry & Purchase Orders	405	22-Jul-16	22-Apr-18	22-Jul-16	21-Apr-18	0	0						
EM3230	Manufacturing & Logistic	286	10-Jul-17	22-Apr-18	10-Jul-17	21-Apr-18	0	0						
Electrical Buildings (EB1, EB2, EB3 & EB4)														
EM3235	Inquiry & Purchase Orders	475	10-Jan-17	29-Apr-18	10-Jan-17	29-Apr-18	0	0						
EM3320	Manufacturing & Logistic (EB4)	390	20-Sep-17	15-Oct-18	21-Sep-17	15-Oct-18	0	0						
DG Store & Chemical Waste Storage Building (DG) and Irrigation & Cleansing Water I														
EM3255	Inquiry & Purchase Orders	328	15-Jan-17	08-Dec-17	15-Jan-17	08-Dec-17	0	0						
Sludge Skip Storage Building (SSSB)														
EM3265	Inquiry & Purchase Orders	215	08-Dec-16	11-Jul-17	08-Dec-16	10-Jul-17	0	0						
EM3270	Manufacturing & Logistic	149	25-Aug-17	20-Jan-18	25-Aug-17	20-Jan-18	0	0						
Re-use Water Building (RW)														
EM3195	Inquiry & Purchase Orders	360	05-Sep-16	09-Mar-18	05-Sep-16	09-Mar-18	0	0						
EM3200	Manufacturing & Logistic	201	20-Aug-17	09-Mar-18	21-Aug-17	09-Mar-18	0	0						
UV Disinfection Facility (UV)														
EM3185	Inquiry & Purchase Orders	595	15-Jul-16	16-Dec-18	15-Jul-16	15-Dec-18	0	0						
EM3190	Manufacturing & Logistic	412	15-Jul-16	31-Aug-17	15-Jul-16	30-Aug-17	0	0						
Cast - In Items														
EM3520	Inquiry & Purchase Orders	449	01-Feb-17	15-Mar-18	01-Feb-17	15-Mar-18	0	0						
EM3535	Delivery of Cast-in Items for SHB	408	01-Feb-17	15-Mar-18	01-Feb-17	15-Mar-18	0	0						
EM3550	Delivery of Cast-in Items for SSSB	68	02-Sep-17	08-Nov-17	02-Sep-17	08-Nov-17	0	0						
EM3555	Delivery of Cast-in Items for Admin. Building	90	13-Sep-17	12-Dec-17	22-Jul-17	19-Oct-17	-53	-53						
EM3560	Delivery of Cast-in Items for DO No. 1	50	06-Sep-17	26-Oct-17	20-Jul-17	07-Sep-17	-49	-49						
EM3570	Delivery of Cast-in Items for CB	84	12-Sep-17	05-Dec-17	13-Aug-17	04-Nov-17	-30	-30						
EM3580	Delivery of Cast-in Items for ICW	91	01-Sep-17	30-Nov-17	01-Aug-17	30-Oct-17	-31	-31						
EM3585	Delivery of Cast-in Items for EB1	75	26-Aug-17	08-Nov-17	27-Jul-17	09-Oct-17	-30	-30						
EM3600	Delivery of Cast-in Items for EB4	136	26-Aug-17	08-Jan-18	26-Aug-17	08-Jan-18	0	0						
EM3605	Delivery of Cast-in Items for RW	57	01-Sep-17	27-Oct-17	01-Aug-17	26-Sep-17	-31	-31						
EM3610	Delivery of Cast-in Items for DG	73	08-Sep-17	19-Nov-17	08-Sep-17	19-Nov-17	0	0						

Appendix D1

Calibration Certificates for Impact Air Quality Monitoring Equipment




Calibration Report
of
High Volume Air Sampler

Manufacturer : Graseby GMW **Date of Calibration** : 23 May 2017
Serial No. : 1934 (ET / EA / 003 / 25) **Calibration Due Date** : 22 July 2017
Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results :	Flow recorder reading (cfm)	58	53	47	40	33
	Qstd (Actual flow rate, m ³ /min)	1.65	1.48	1.28	1.03	0.83
	Pressure : 770.31 mm Hg	Temp. : 298 K				

Sampler 1934 Calibration Curve
Site: San Wai (ASR1a)

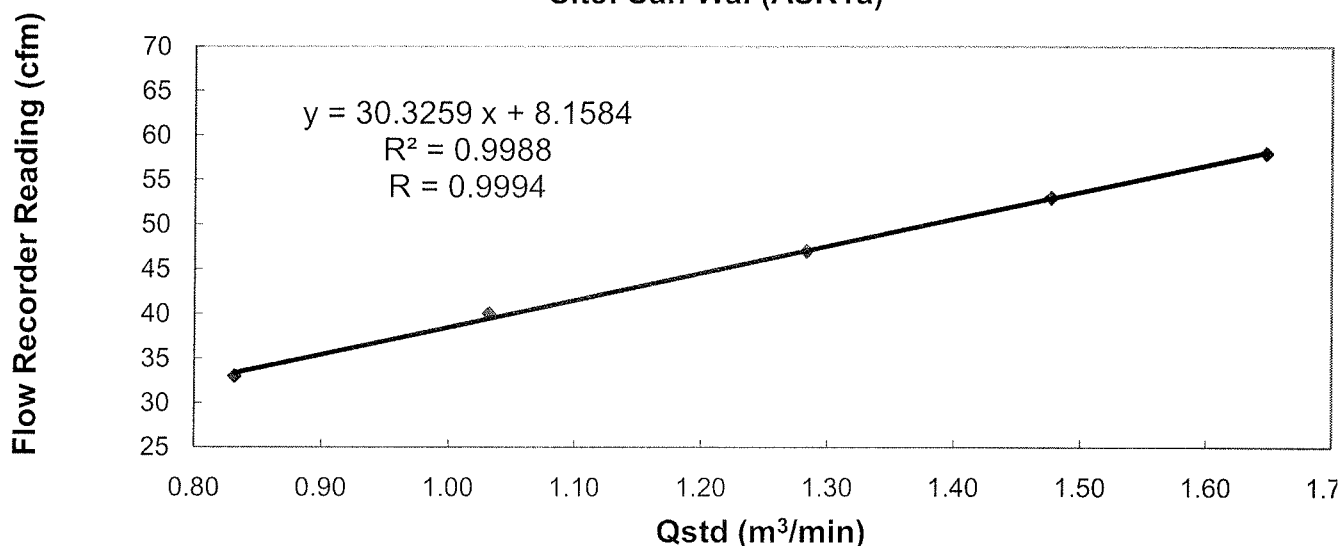

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.


The high volume sampler complies* / ~~does not comply*~~ with the specified requirements and is deemed acceptable* / unacceptable* for use.

Calibrated by :

CHAN, Wai Man
(Technician)

Approved by :

LAW, Sau Yee
(Senior Environmental Officer)



Calibration Report
of
High Volume Air Sampler


Manufacturer : Graseby (Model No. GS2310) **Date of Calibration** : 23 May 2017

Serial No. : 9998 (ET / EA / 003 / 12) **Calibration Due Date** : 22 July 2017

Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results	Flow recorder reading (cfm)	52	47	40	33	27
	Qstd (Actual flow rate, m ³ /min)	1.78	1.59	1.38	1.13	0.87
	Pressure : 771.06 mm Hg	Temp. : 298 K				

Sampler 9998 Calibration Curve
Site: San Wai (ASR2a)

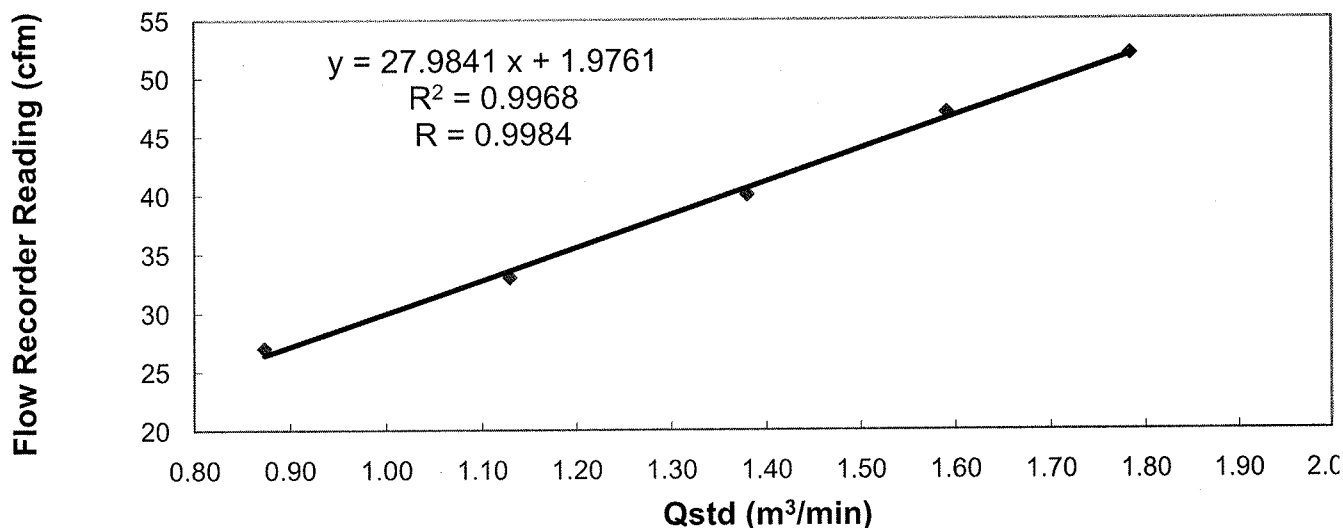

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.


The high volume sampler complies* / ~~does not comply*~~ with the specified requirements and is deemed acceptable* / unacceptable* for use.

Calibrated by :

CHAN, Wai Man
(Technician)

Checked by :

LAW, Sau Yee
(Senior Environmental Officer)



Internal Calibration Report


of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 31 March 2017

Serial No. : 135261 (ET/EA/001/08) **Calibration Due Date** : 30 September 2017

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition

Results :	Dust Monitor (CPM)	36	70	180
	High Volume Air Sampler (ug/m ³)	50	113	270
	High Volume Air Sampler Serial No.:1177		Calibration Due Date: 23 April 2017	

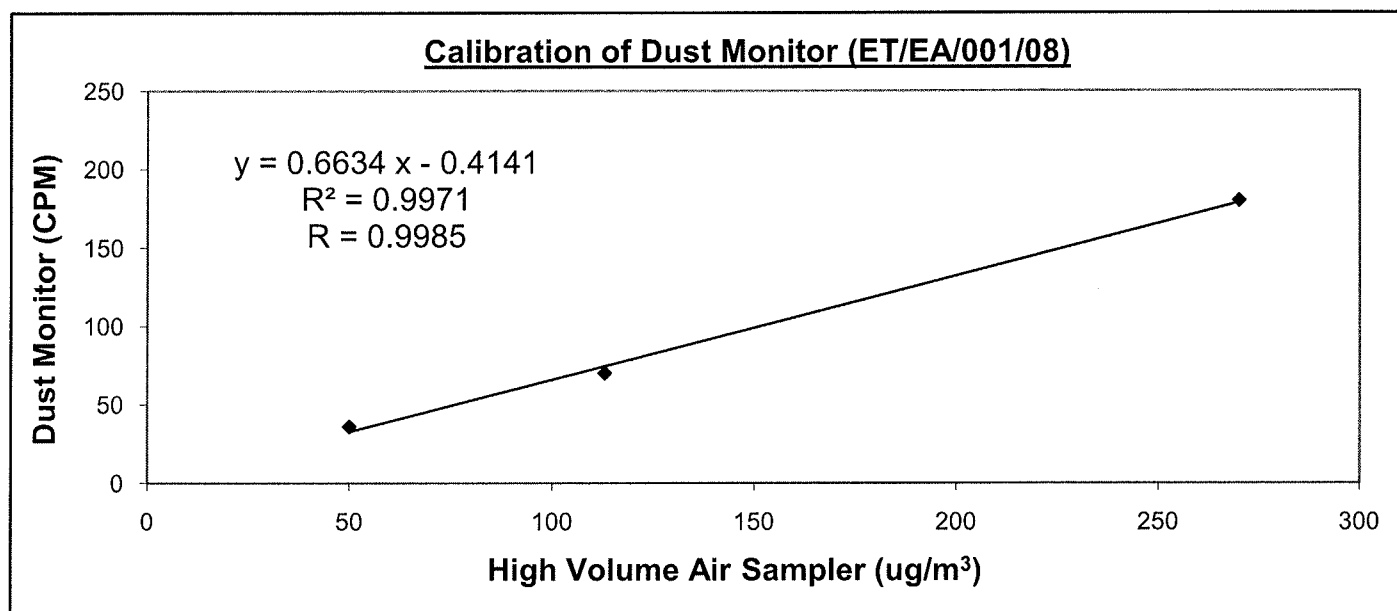


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after three-point calibration


The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / ~~unacceptable~~ * for use.

Calibrated by :


Chung Ka Ho
(Technician)

Checked by :


LAW, Sau Yee
(Senior Environmental Officer)




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 24 December 2016

Serial No. : 1Z5635 (ET/EA/001/10) **Calibration Due Date** : 23 June 2017

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition


Results	Dust Monitor (CPM)	45	83	199
	High Volume Air Sampler (ug/m ³)	60	142	299
	High Volume Air Sampler Serial No.: 1177 Calibration Due Date: 23 February 2017			

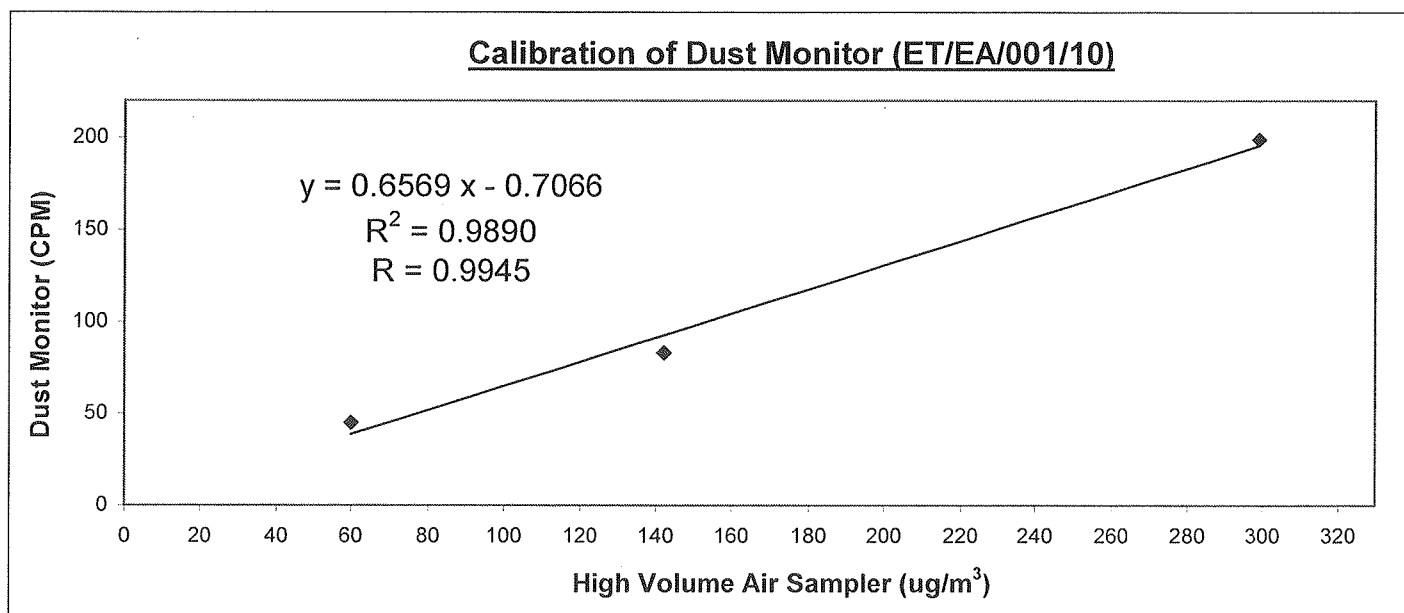


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / does not comply * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : 
CHUNG, Kit Yu
(Technician)

Checked by : 
LAW, Sau Yee
(Senior Environmental Officer)



Internal Calibration Report
of
Dust Monitor


Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 24 June 2017

Serial No. : 1Z5635 (ET/EA/001/10) **Calibration Due Date** : 23 December 2017

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition

Results	Dust Monitor (CPM)	44	88	200
	High Volume Air Sampler (ug/m ³)	59	145	300
	High Volume Air Sampler Serial No.: 1177 Calibration Due Date: 16 August 2017			

Calibration of Dust Monitor (ET/EA/001/10)

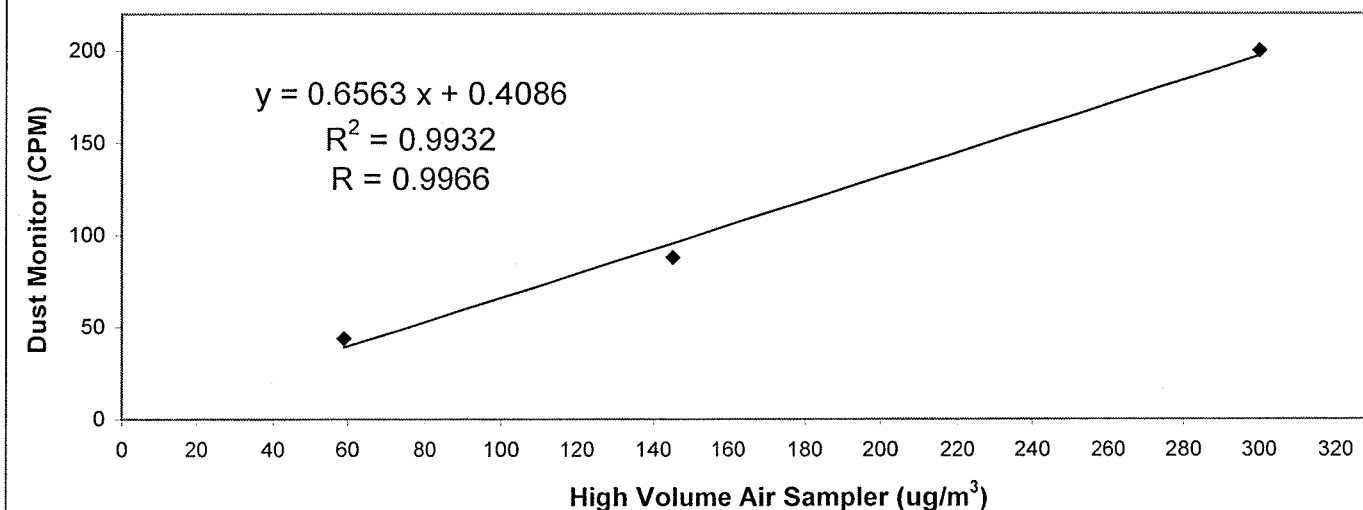

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration


The Dust Trak Monitor complies * / does not comply * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by :

CHUNG, Ka Ho
(Technician)

Checked by :

LAW, Sau Yee
(Senior Environmental Officer)




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration :** 23 January 2017

Serial No. : 597340 (ET/EA/001/14) **Calibration Due Date :** 22 July 2017


Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition


Results :	Dust Monitor (CPM)	28	50	170
	High Volume Air Sampler (ug/m ³)	35	100	272
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 22 February 2017	

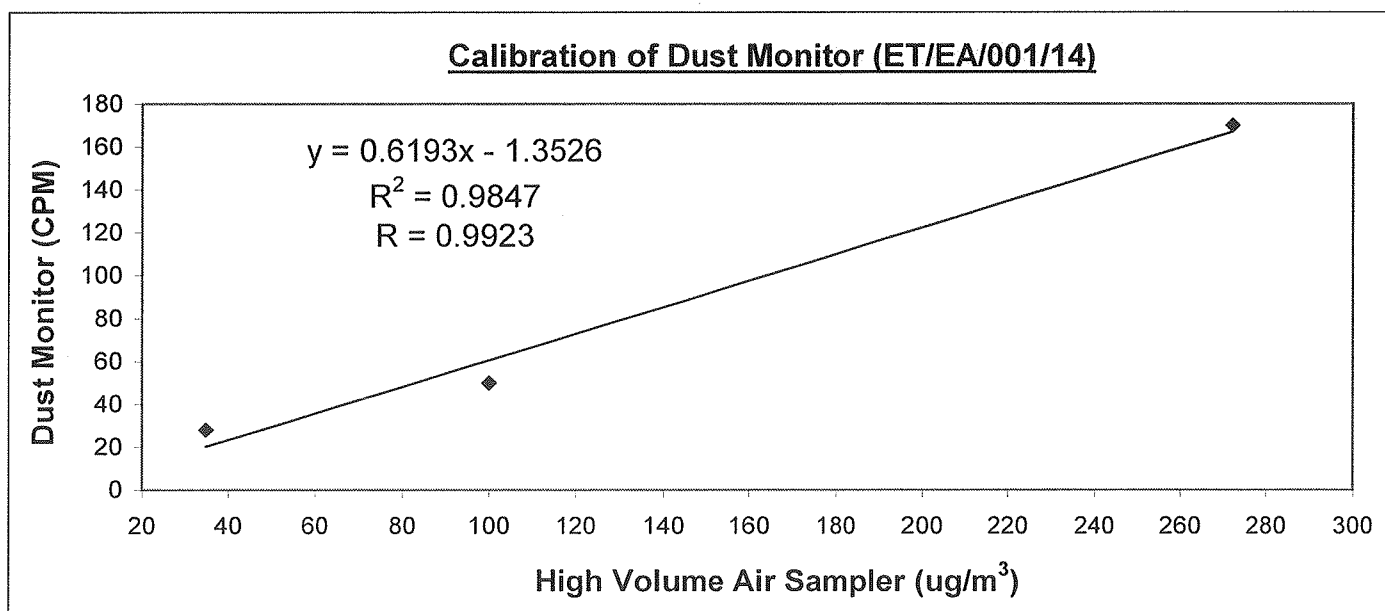


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : 
CHUNG, Ka Ho
(Technician)

Checked by : 
LAW, Sau Yee
(Senior Environmental Officer)




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 23 January 2017

Serial No. : 597227 (ET/EA/001/15) **Calibration Due Date** : 22 July 2017


Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition


Results	Dust Monitor (CPM)	29	65	170
	High Volume Air Sampler (ug/m ³)	32	115	262
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 22 February 2017	

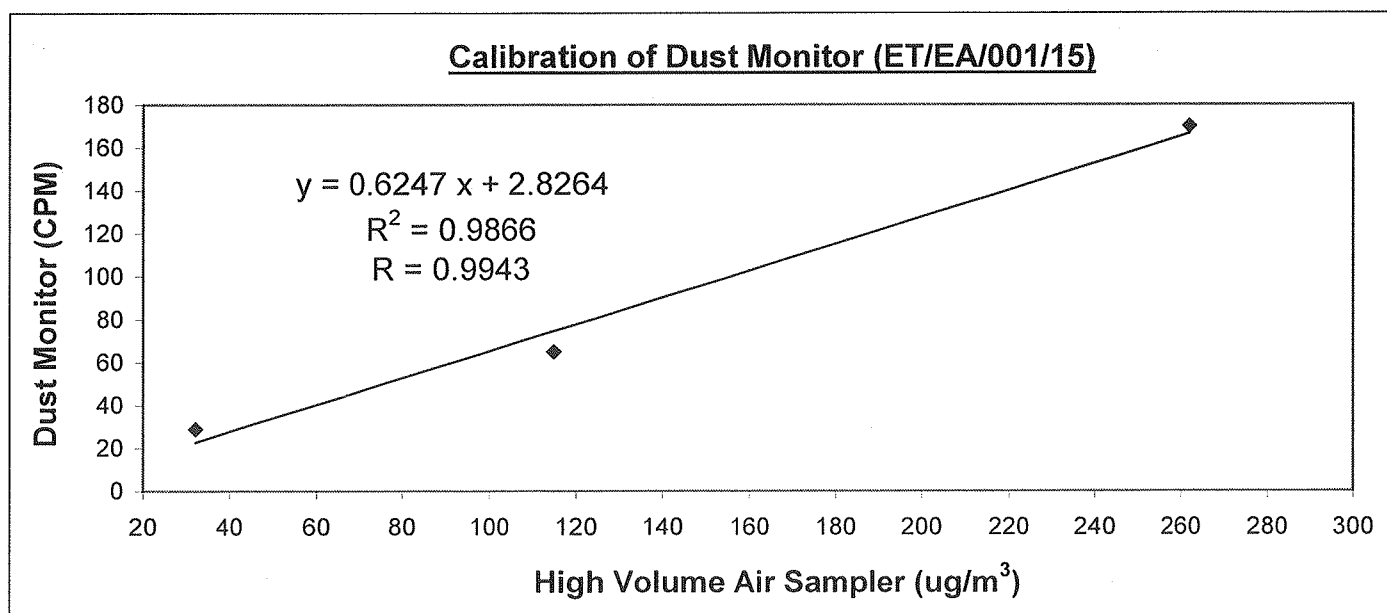

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : 
CHUNG, Ka Ho
(Technician)

Checked by : 
LAW, Sau Yee
(Senior Environmental Officer)



ET/EA/004/13

TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE
 VILLAGE OF CLEVELAND, OH
 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Apr 12, 2016 Rootmeter S/N 0438320 Ta (K) - 294
 Operator Tisch Orifice I.D. - 3163 Pa (mm) - 758.19

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1	NA	NA	1.00	1.4390	3.2	2.00
2	NA	NA	1.00	1.0280	6.4	4.00
3	NA	NA	1.00	0.9160	7.9	5.00
4	NA	NA	1.00	0.8760	8.7	5.50
5	NA	NA	1.00	0.7240	12.7	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
1.0069	0.6997	1.4221	0.9958	0.6920	0.8806
1.0027	0.9754	2.0112	0.9916	0.9646	1.2454
1.0006	1.0923	2.2485	0.9895	1.0802	1.3924
0.9996	1.1411	2.3583	0.9885	1.1284	1.4604
0.9942	1.3732	2.8442	0.9832	1.3580	1.7613
Qstd slope (m) = 2.11024			Qa slope (m) = 1.32140		
intercept (b) = -0.05237			intercept (b) = -0.03243		
coefficient (r) = 0.99995			coefficient (r) = 0.99995		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

Vstd = Diff. Vol [(Pa-Diff. Hg)/760] (298/Ta)
 Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
 Qa = Va/Time

For subsequent flow rate calculations:

Qstd = 1/m{ [SQRT(H2O(Pa/760) (298/Ta))] - b}
 Qa = 1/m{ [SQRT H2O(Ta/Pa)] - b}

Appendix D2

Impact Air Quality Monitoring Results

Summary of Impact 1-hour TSP Monitoring Results

Air Quality Monitoring Station : ASR1a

Date	Weather	Temperature (°C)	Monitoring Period		1-hr TSP ($\mu\text{g}/\text{m}^3$)
			Start	Finish	
6/6/2017	Fine	33	13:17	14:17	71
6/6/2017	Fine	33	14:17	15:17	80
6/6/2017	Fine	34	15:17	16:17	63
12/6/2017	Cloudy	30	09:00	10:00	64
12/6/2017	Cloudy	30	10:00	11:00	60
12/6/2017	Cloudy	30	11:00	12:00	65
17/6/2017	Drizzle	28	08:00	09:00	65
17/6/2017	Drizzle	28	09:00	10:00	60
17/6/2017	Drizzle	28	10:00	11:00	62
23/6/2017	Fine	31	11:00	12:00	71
23/6/2017	Fine	31	13:00	14:00	72
23/6/2017	Fine	31	14:00	15:00	68
29/6/2017	Fine	31	15:38	16:38	61
29/6/2017	Fine	31	16:38	17:38	56
29/6/2017	Fine	31	17:38	18:38	64
Min					56
Max					80
Average					65

Air Quality Monitoring Station : ASR2a

Date	Weather	Temperature (°C)	Monitoring Period		1-hr TSP (mg/m^3)
			Start	Finish	
6/6/2017	Fine	31	08:51	09:51	81
6/6/2017	Fine	32	09:51	10:51	94
6/6/2017	Fine	33	10:51	11:51	86
12/6/2017	Cloudy	30	13:00	14:00	70
12/6/2017	Cloudy	30	14:00	15:00	68
12/6/2017	Cloudy	30	15:00	16:00	60
17/6/2017	Drizzle	28	08:30	09:30	55
17/6/2017	Drizzle	28	09:30	10:30	52
17/6/2017	Drizzle	28	10:30	11:30	58
23/6/2017	Fine	31	10:55	11:55	73
23/6/2017	Fine	31	13:05	14:05	78
23/6/2017	Fine	31	14:04	15:05	70
29/6/2017	Fine	31	15:45	16:45	65
29/6/2017	Fine	31	16:45	17:45	69
29/6/2017	Fine	31	17:45	18:45	63
Min					52
Max					94
Average					69

Summary of Impact 24-hour TSP Monitoring Results

Air Quality Monitoring Station : ASR1a

Start		Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Paper Weight (g)		Conc. (μg/m ³)	Weather Condition
Date	Time	Date	Time	Initial	Final		Initial	Final		Initial	Final		
6/6/2017	13:30	7/6/2017	13:30	22925.64	22949.64	24	0.8521	0.8521	0.8521	2.7496	3.0039	207	Fine
12/6/2017	09:00	13/6/2017	09:00	22949.64	22973.64	24	0.8521	0.8521	0.8521	2.7743	3.0088	191	Cloudy
17/6/2017	11:05	18/6/2017	11:05	22973.64	22997.64	24	0.8521	0.8521	0.8521	2.7685	2.9820	174	Cloudy
23/6/2017	13:00	24/6/2017	13:00	22997.64	23021.64	24	0.8521	0.8521	0.8521	2.8051	3.0251	179	Fine
29/6/2017	15:42	30/6/2017	15:42	23021.64	23045.64	24	0.8521	0.8521	0.8521	2.7845	2.9790	159	Fine
											Min	159	
											Max	207	
											Average	182	


Air Quality Monitoring Station : ASR2a

Start		Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Weight (g)		Conc. (μg/m ³)	Weather Condition
Date	Time	Date	Time	Initial	Final		Initial	Final		Initial	Final		
6/6/2017	09:00	7/6/2017	09:00	19886.45	19910.45	24	1.1444	1.1444	1.1444	2.8001	3.0512	152	Fine
12/6/2017	13:10	13/6/2017	13:10	19910.45	19934.45	24	1.1444	1.1444	1.1444	2.7645	3.0081	148	Cloudy
17/6/2017	11:25	18/6/2017	11:25	19934.45	19958.45	24	1.1444	1.1444	1.1444	2.8042	3.0550	152	Cloudy
23/6/2017	13:30	24/6/2017	13:30	19958.45	19982.45	24	1.1444	1.1444	1.1444	2.7845	3.0458	159	Fine
29/6/2017	16:15	30/6/2017	16:15	19982.45	20006.45	24	1.1444	1.1444	1.1444	2.7643	3.0244	158	Fine
											Min	148	
											Max	159	
											Average	154	


Appendix D3

Graphical Plots of Impact Air Quality Monitoring Results


1-hr TSP at ASR1a

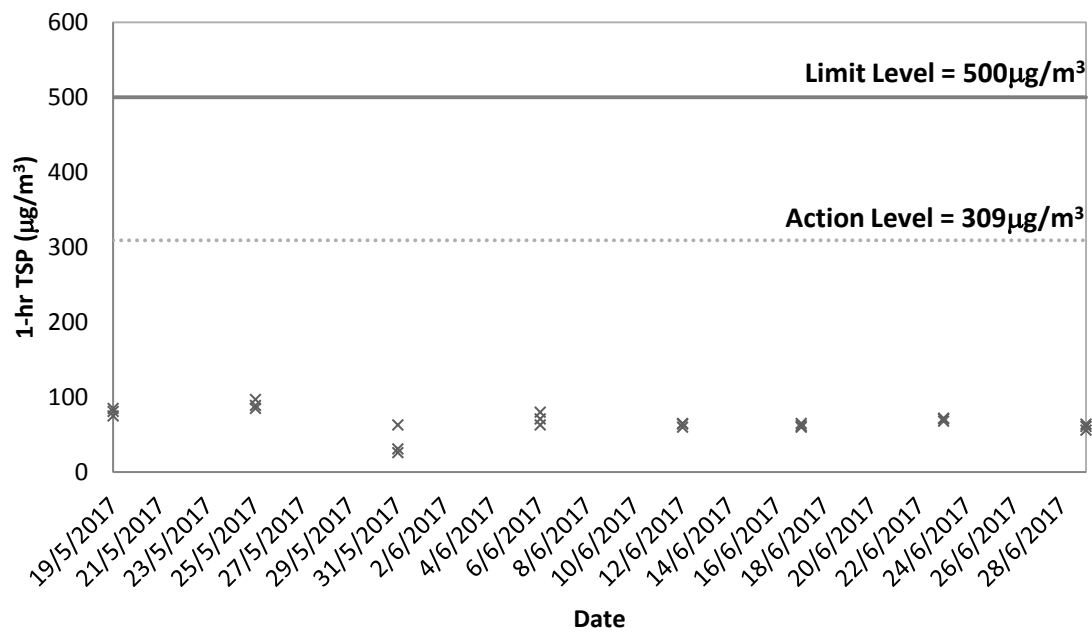


1-hr TSP at ASR2a

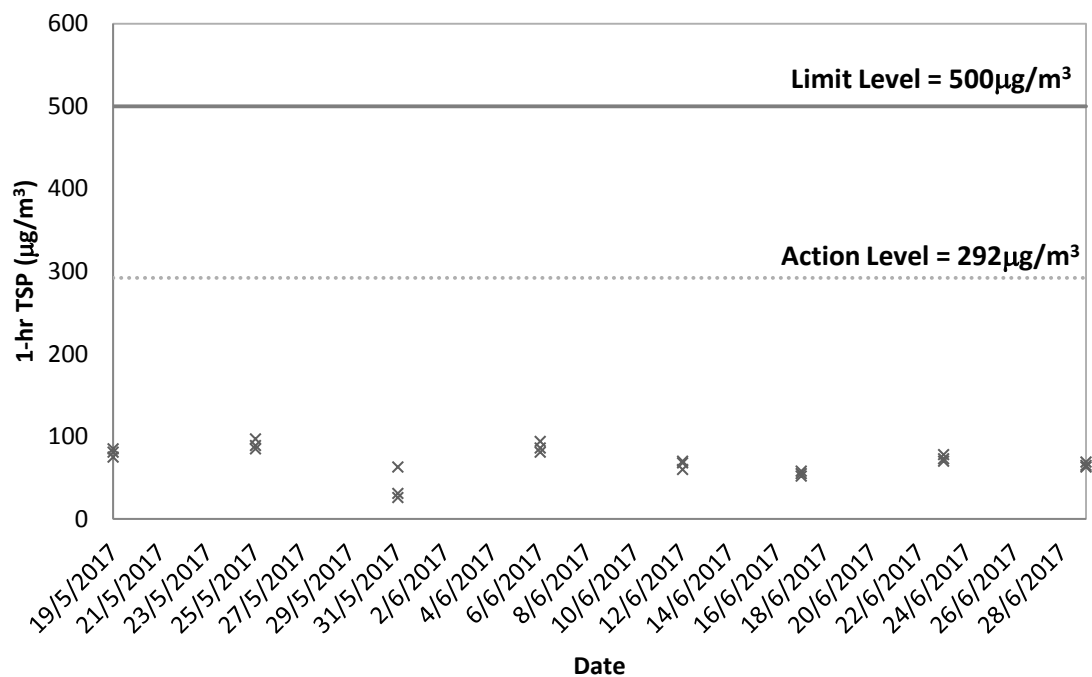

24-hr TSP at ASR1a

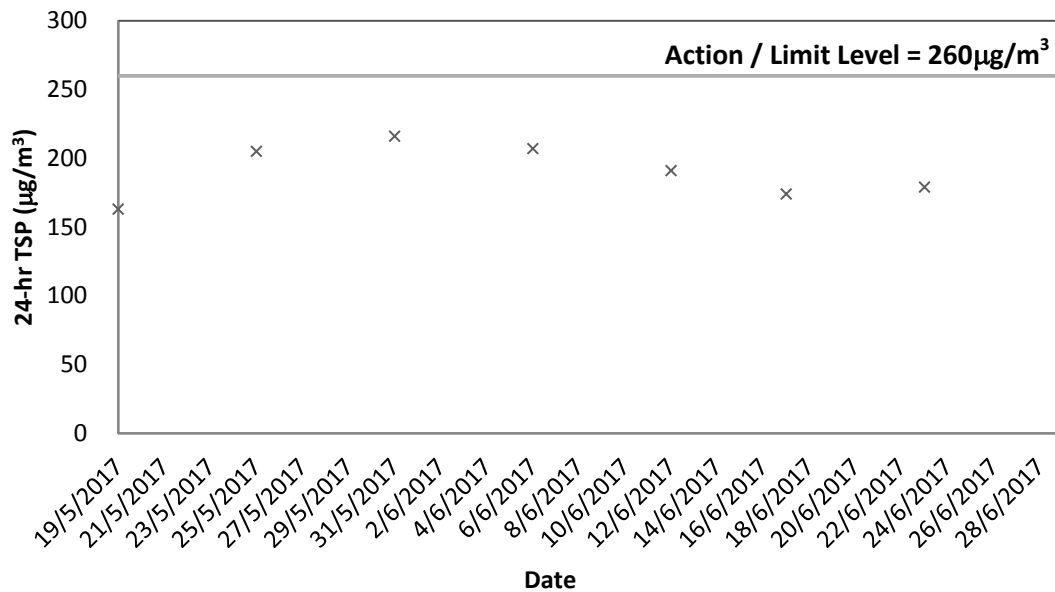

24-hr TSP at ASR2a

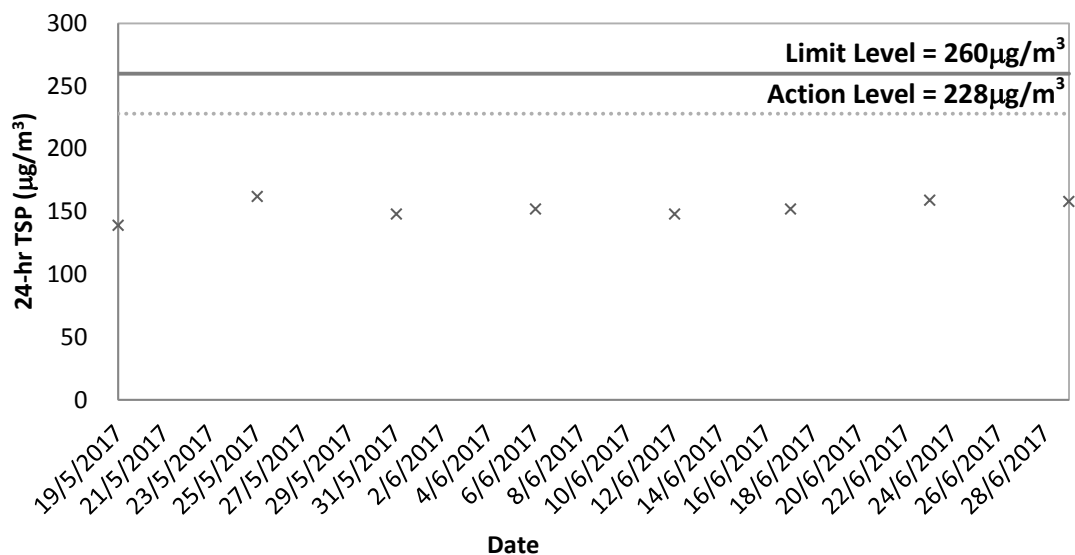



Appendix E1

Calibration Certificates for Impact Noise Monitoring Equipment



Calibration Certificate

Certificate No. **610324**

Page 1 of 3 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q64225

Date of receipt : 15-Nov-16

Item Tested

Description : Sound Level Meter

Manufacturer : Rion

I.D. : ET/EN/003/14

Model : NL-52

Serial No. : 00320645

Test Conditions

Date of Test : 24-Nov-16

Supply Voltage : --

Ambient Temperature : (23 ± 3)°C

Relative Humidity : (50 ± 25) %

Test Specifications

Calibration check.

Ref. Document/Procedure : Z01, IEC 61672.

Test Results

All results were within the IEC 61672 Type 1 specification.

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S017	Multi-Function Generator	C147450	SCL-HKSAR
S240	Sound Level Calibrator	601604	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by :

Kin Wong

Approved by :

Alan Chu

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

Date: 24-Nov-16



Calibration Certificate

Certificate No. 610324

Page 2 of 3 Pages

Results :

1. Self-generated noise: 16.5 dBA (Mfr's Spec ≤ 17 dBA)

2. Acoustical signal test

UUT Setting				Applied Value (dB)	UUT Reading (dB)
Range (dB)	Frequency Weighting	Time Weighting	Octave Filter		
30-130	A	F	OFF	94.0	94.0
		S	OFF		94.0
	C	F	OFF		94.1
	Z	F	OFF		94.1
	A	F	OFF	114.0	114.0
		S	OFF		114.0
	C	F	OFF		114.1
	Z	F	OFF		114.1

IEC 61672 Type 1 Spec. : ± 1.1 dB

Uncertainty : ± 0.1 dB

3 Electrical signal tests of frequency weightings (A weighting)

Frequency	Attenuation (dB)	IEC 61672 Type 1 Spec.
31.5 Hz	-39.5	- 39.4 dB, ± 2 dB
63 Hz	-26.2	- 26.2 dB, ± 1.5 dB
125 Hz	-16.1	- 16.1 dB, ± 1.5 dB
250 Hz	-8.6	- 8.6 dB, ± 1 dB
500 Hz	-3.2	- 3.2 dB, ± 1.4 dB
1 kHz	0.0 (Ref)	0 dB, ± 1.1 dB
2 kHz	+1.1	+ 1.2 dB, ± 1.6 dB
4 kHz	+0.7	+ 1.0 dB, ± 1.6 dB
8 kHz	-1.1	- 1.1 dB, + 2.1 dB \sim -3.1 dB
16 kHz	-8.5	- 6.6 dB, + 3.5 dB \sim - 17.0 dB

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 610324

Page 3 of 3 Pages

4. Frequency & Time weightings at 1 kHz

4.1 Frequency Weighting (Fast)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
A	94.0	94.0 (Ref.)	- -	± 0.4 dB
C	94.0	94.1	+0.1	
Z	94.0	94.1	+0.1	

4.2 Time Weighting (A-weighted)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
Fast	94.0	94.0 (Ref.)	- -	± 0.3 dB
Slow	94.0	94.0	0.0	
Time-averaging	94.0	94.0	0.0	

Uncertainty : ± 0.1 dB

Remarks : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1025 hPa.

4. Preamplifier model : NH-25 , S/N : 10653

5. Firmware Version: 1.2

6. Power Supply Check: OK

7. The UUT was adjusted with the laboratory's sound calibrator at the reference sound pressure level before the calibration.

----- END -----



Calibration Certificate

Certificate No. 701813

Page 1 of 3 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q70792

Date of receipt : 2-Mar-17

Item Tested

Description : Sound Level Meter

Manufacturer : Rion

Model : NL-52

I.D. : ET/EN/003/17

Serial No. : 00264519

Test Conditions

Date of Test : 7-Mar-17

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Supply Voltage : --

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure: Z01, IEC 61672.

Test Results

All results were within the IEC 61672 Type 1 specification.

The results are shown in the attached page(s).

Main Test equipment used:

Equipment No.	Description	Cert. No.	Traceable to
S017	Multi-Function Generator	C170120	SCL-HKSAR
S240	Sound Level Calibrator	701036	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by : 
Kin Wong

Approved by : 
Alan Chu

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

Date: 7-Mar-17



Calibration Certificate

Certificate No. 701813

Page 2 of 3 Pages

Results :

1. Self-generated noise: 15.9 dBA (Mfr's Spec ≤ 17 dBA)

2. Acoustical signal test

UUT Setting				Applied Value (dB)	UUT Reading (dB)
Range (dB)	Frequency Weighting	Time Weighting	Octave Filter		
30-130	A	F	OFF	94.0	94.0
		S	OFF		94.0
	C	F	OFF		94.1
	Z	F	OFF		94.1
	A	F	OFF	114.0	114.1
		S	OFF		114.1
	C	F	OFF		114.1
	Z	F	OFF		114.1

IEC 61672 Type 1 Spec. : ± 1.1 dB

Uncertainty : ± 0.1 dB

3 Electrical signal tests of frequency weightings (A weighting)

Frequency	Attenuation (dB)	IEC 61672 Type 1 Spec.
31.5 Hz	-39.7	- 39.4 dB, ± 2 dB
63 Hz	-26.2	- 26.2 dB, ± 1.5 dB
125 Hz	-16.2	- 16.1 dB, ± 1.5 dB
250 Hz	-8.7	- 8.6 dB, ± 1 dB
500 Hz	-3.2	- 3.2 dB, ± 1.4 dB
1 kHz	0.0 (Ref)	0 dB, ± 1.1 dB
2 kHz	+1.2	+ 1.2 dB, ± 1.6 dB
4 kHz	+1.0	+ 1.0 dB, ± 1.6 dB
8 kHz	-1.1	- 1.1 dB, + 2.1 dB \sim -3.1 dB
16 kHz	-8.0	- 6.6 dB, + 3.5 dB \sim - 17.0 dB

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 701813

Page 3 of 3 Pages

4. Frequency & Time weightings at 1 kHz

4.1 Frequency Weighting (Fast)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
A	94.0	94.0 (Ref.)	--	± 0.4 dB
C	94.0	94.1	+0.1	
Z	94.0	94.1	+0.1	

4.2 Time Weighting (A-weighted)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
Fast	94.0	94.0 (Ref.)	--	± 0.3 dB
Slow	94.0	94.0	0.0	
Time-averaging	94.0	94.0	0.0	

Uncertainty : ± 0.1 dB

Remarks : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1012 hPa.

4. Preamplifier model : NH-25 , S/N : 64644

5. Firmware Version: 1.7

6. Power Supply Check: OK

7. The UUT was adjusted with the laboratory's sound calibrator at the reference sound pressure level before the calibration.

----- END -----



Calibration Certificate

Certificate No. **609158**

Page 1 of 2 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q63739

Date of receipt : 7-Oct-16

Item Tested

Description : Sound Level Calibrator

Manufacturer : Rion

I.D. : ET/EN/002/01

Model : NC-73

Serial No. : 10196943

Test Conditions

Date of Test : 24-Oct-16

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure : F21, Z02.

Test Results

All results were within the manufacturer's specification.

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S014	Spectrum Analyzer	605758	NIM-PRC & SCL-HKSAR
S240	Sound Level Calibrator	601604	NIM-PRC & SCL-HKSAR
S041	Universal Counter	607883	SCL-HKSAR
S206	Sound Level Meter	605757	SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by : 
Kin Wong

Approved by : 
Alan Chu

This Certificate is issued by:
Hong Kong Calibration Ltd.
Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.
Tel: 2425 8801 Fax: 2425 8646

Date: 24-Oct-16



Calibration Certificate

Certificate No. **609158**

Page 2 of 2 Pages

Results :

1. Level Accuracy (at 1 kHz)

UUT Nominal Value	Measured Value	Mfr's Spec.
94 dB	94.0 dB	± 1 dB

Uncertainty : ± 0.2 dB

2. Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's Spec.
1 kHz	0.993 kHz	± 2 %

Uncertainty : ± 0.1 %

3. Level Stability : 0.0 dB

Uncertainty : ± 0.01 dB

4. Total Harmonic Distortion : < 0.4 %

Mfr's Spec. : < 3 %

Uncertainty : ± 2.3 % of reading

Remarks: 1. UUT : Unit-Under-Test
2. The uncertainty claimed is for a confidence probability of not less than 95%.
3. Atmospheric Pressure : 1020 hPa

----- END -----



Calibration Certificate

Certificate No. 700818

Page 1 of 2 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q70345

Date of receipt : 25-Jan-17

Item Tested

Description : Thermo-Anemometer

Manufacturer : AZ Instrument

Model : AZ 8908

I.D. : ET/EN/001/05

Serial No. : 1064869

Test Conditions

Date of Test : 15-Feb-17

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure: T03, Z04.

Test Results

A correction factor of x 1.06 is required to bring the meter reading to within the manufacturer's specification.
The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S155	Std. Anemometer	611074	NIM-PRC
S223C	Std. Thermometer	604664	NIM-PRC

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by :

C H Chan

Approved by :

Steve Kwan

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

Date: 15-Feb-17



Calibration Certificate

Certificate No. 700818

Page 2 of 2 Pages

Results :

1. Velocity

Applied Value (m/s)	UUT Reading (m/s)	Corrected Reading (UUT Reading x 1.06)	Mfr's Spec.
0.00	0.0	0.0	± 5 % of reading.
2.50	2.4	2.5	
5.00	4.8	5.1	
10.00	* 9.3	9.9	
15.00	* 13.6	14.4	
19.00	* 17.2	18.2	

2. Temperature

Applied Value (°C)	UUT Reading (°C)	Mfr's Spec.
22.85	22.5	± 1 °C

Remark : 1. UUT: Unit-Under-Test

2. Uncertainty : ± (0.9% + 0.16 m/s) for Velocity, ± 0.1 °C for Temperature, for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1 022 hPa

4. * Out of specification

----- END -----

Appendix E2

Impact Noise Monitoring Results

Day-time Noise Monitoring

Monitoring Station: NSR1a

Date	Weather	Temperature (°C)	Start Time (hh:mm)	End Time (hh:mm)	Noise Level at NSR1a, dB (A)			Wind Speed (m/s)
					Leq (30min)	L10 (30min)	L90 (30min)	
06/06/17	Fine	33	13:16	13:46	59.5	63.0	49.2	0.2
12/06/17	Cloudy	30	09:00	09:30	59.6	62.7	54.1	0.2
17/06/17	Drizzle	28	10:00	10:30	71.7	74.3	59.3	0.4
23/06/17	Fine	31	13:00	13:30	70.5	74.2	65.3	0.2
29/06/17	Fine	31	15:35	16:05	57.0	60.4	50.3	0.2
Min					57.0	60.4	49.2	
Max					71.7	74.3	65.3	
Logarithmic Average for normal weekdays					67.5	70.7	59.7	

Monitoring Station: NSR2a(*)


Date	Weather	Temperature (°C)	Start Time (hh:mm)	End Time (hh:mm)	Noise Level at NSR2a, dB (A)			Wind Speed (m/s)
					Leq (30min)	L10 (30min)	L90 (30min)	
06/06/17	Fine	31	08:52	09:22	64.3	68.7	54.1	0.2
12/06/17	Cloudy	30	13:00	13:30	64.8	66.3	60.7	0.3
17/06/17	Drizzle	28	10:40	11:10	68.2	70.3	62.8	0.6
23/06/17	Fine	31	13:45	14:15	69.9	72.8	64.6	0.2
29/06/17	Fine	31	16:07	16:37	62.4	64.1	58.3	0.3
Min					62.4	64.1	54.1	
Max					69.9	72.8	64.6	
Logarithmic Average for normal weekdays					66.8	69.4	61.4	

(*) : 3dB(A) correction was added to the results during the free-field noise measurements


Appendix E3

Graphical Plots of Impact Noise Monitoring Data

Noise Level at NSR1a

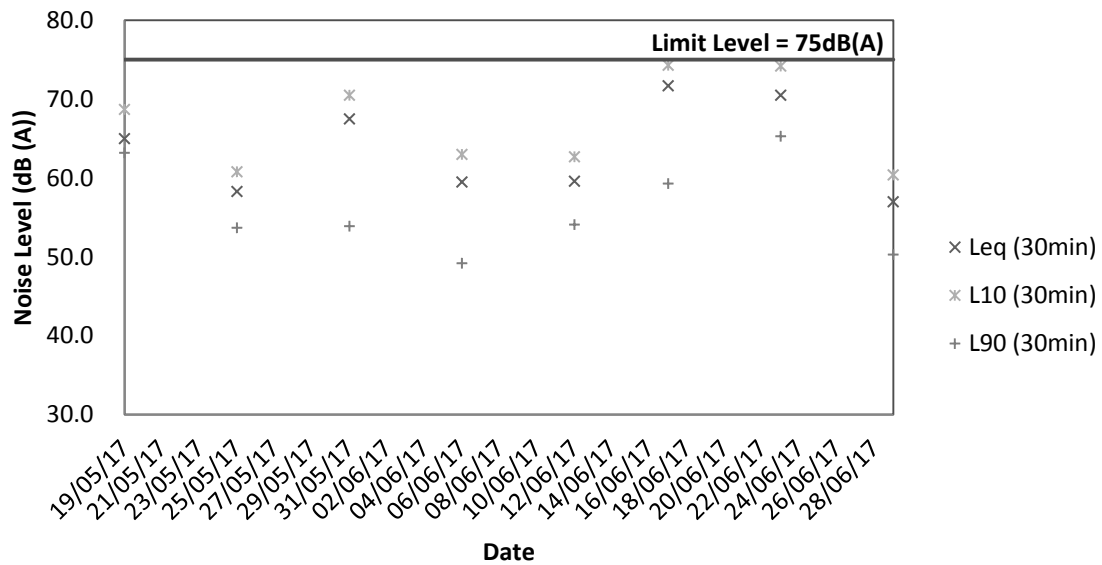

Noise Level at NSR2a

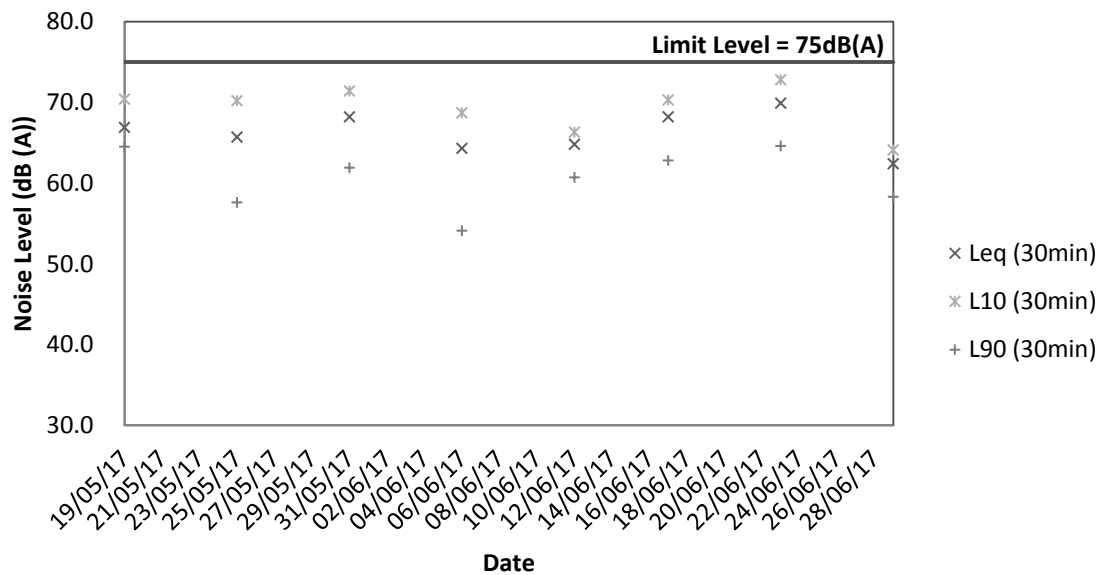

Appendix F1

Calibration Certificates for Impact Water Quality Monitoring Equipments



Performance Check of Turbidity Meter

Equipment Ref. No. : ET/0505/014 Manufacturer : HACH

Model No. : 2100Q Serial No. : 13110C029448

Date of Calibration : 22/05/2017 Due Date : 21/08/2017

Theoretical Value of Turbidity Standard (NTU)	Measured Value (NTU)	Difference % *
20	20.8	4.0
100	103	3.0
800	823	2.9

(*) Difference = (Measured Value – Theoretical Value) / Theoretical Value x 100

Acceptance Criteria

Difference : -5 % to 5 %

The turbidity meter complies * / ~~does not comply~~ * with the specified requirements and is deemed acceptable * / ~~unacceptable~~ * for use. Measurements are traceable to national standards.

Prepared by :

Checked by :



Internal Calibration Report of Dissolved Oxygen Meter

Equipment Ref. No. : <u>ET/EW/008/008</u>	Manufacturer : <u>YSI</u>
Model No. : <u>Pro 2030</u>	Serial No. : <u>14M101489</u>
Date of Calibration : <u>22/04/2017</u>	Calibration Due Date : <u>21/07/2017</u>

Temperature Verification

Ref. No. of Reference Thermometer : ET/0521/017

Ref. No. of Water Bath : ---

Temperature (°C)				
Reference Thermometer reading	Measured	20.3	Corrected	19.8
DO Meter reading	Measured	19.7	Difference	0.1

Standardization of sodium thiosulphate ($\text{Na}_2\text{S}_2\text{O}_3$) solution

Reagent No. of $\text{Na}_2\text{S}_2\text{O}_3$ titrant	CPE/012/4.5/001/15	Reagent No. of 0.025N $\text{K}_2\text{Cr}_2\text{O}_7$	CPE/012/4.4/002/18
	Trial 1		Trial 2
Initial Vol. of $\text{Na}_2\text{S}_2\text{O}_3$ (ml)	0.00		10.15
Final Vol. of $\text{Na}_2\text{S}_2\text{O}_3$ (ml)	10.15		20.35
Vol. of $\text{Na}_2\text{S}_2\text{O}_3$ used (ml)	10.15		10.20
Normality of $\text{Na}_2\text{S}_2\text{O}_3$ solution (N)	0.02463		0.02451
Average Normality (N) of $\text{Na}_2\text{S}_2\text{O}_3$ solution (N)	0.02457		
Acceptance criteria, Deviation	Less than $\pm 0.001\text{N}$		

Calculation: Normality of $\text{Na}_2\text{S}_2\text{O}_3$, $N = 0.25 / \text{ml } \text{Na}_2\text{S}_2\text{O}_3 \text{ used}$

Linearity Checking

Determination of dissolved oxygen content by Winkler Titration *

Purging Time (min)	2		5		10	
Trial	1	2	1	2	1	2
Initial Vol. of $\text{Na}_2\text{S}_2\text{O}_3$ (ml)	0.00	10.90	21.80	0.00	6.80	10.60
Final Vol. of $\text{Na}_2\text{S}_2\text{O}_3$ (ml)	10.90	21.80	28.60	6.80	10.60	14.50
Vol. (V) of $\text{Na}_2\text{S}_2\text{O}_3$ used (ml)	10.90	10.90	6.80	6.80	3.80	3.90
Dissolved Oxygen (DO), mg/L	7.19	7.19	4.49	4.49	2.51	2.57
Acceptance criteria, Deviation	Less than + 0.3mg/L		Less than + 0.3mg/L		Less than + 0.3mg/L	

Calculation: $\text{DO (mg/L)} = V \times N \times 8000/298$

Purging time, min	DO meter reading, mg/L			Winkler Titration result *, mg/L			Difference (%) of DO Content
	1	2	Average	1	2	Average	
2	7.23	7.19	7.21	7.19	7.19	7.19	0.28
5	4.43	4.40	4.42	4.49	4.49	4.49	1.57
10	2.48	2.51	2.50	2.51	2.57	2.54	1.59
Linear regression coefficient				0.9998			



Internal Calibration Report of Dissolved Oxygen Meter

Zero Point Checking

DO meter reading, mg/L	0.00
------------------------	------

Salinity Checking

Reagent No. of NaCl (10ppt)	CPE/012/4.7/004/1	Reagent No. of NaCl (30ppt)	CPE/012/4.8/004/1
-----------------------------	-------------------	-----------------------------	-------------------

Determination of dissolved oxygen content by Winkler Titration **

Salinity (ppt)	10		30	
Trial	1	2	1	2
Initial Vol. of Na ₂ S ₂ O ₃ (ml)	0.00	10.70	21.30	30.70
Final Vol. of Na ₂ S ₂ O ₃ (ml)	10.70	21.30	30.70	40.20
Vol. (V) of Na ₂ S ₂ O ₃ used (ml)	10.70	10.60	9.40	9.50
Dissolved Oxygen (DO), mg/L	7.06	6.99	6.20	6.27
Acceptance criteria, Deviation	Less than + 0.3mg/L		Less than + 0.3mg/L	

Calculation: DO (mg/L) = V x N x 8000/298

Salinity (ppt)	DO meter reading, mg/L			Winkler Titration result**, mg/L			Difference (%) of DO Content
	1	2	Average	1	2	Average	
10	7.00	6.97	6.99	7.06	6.99	7.03	0.57
30	6.07	6.11	6.09	6.20	6.27	6.24	2.43

Acceptance Criteria

- (1) Difference between temperature readings from temperature sensor of DO probe and reference thermometer : < 0.5 °C
- (2) Linear regression coefficient : > 0.99
- (3) Zero checking: 0.0mg/L
- (4) Difference (%) of DO content from the meter reading and by winkler titration : within ± 5%

The equipment complies # / ~~does not comply~~ # with the specified requirements and is deemed acceptable #
/ unacceptable # for use.

Delete as appropriate

Calibrated by : 

Approved by : 

Appendix F2

Impact Water Quality Monitoring Results

Impact Water Quality Monitoring

Monitoring Station: R1b


Date	Sampling Duration	Weather Condition	Sampling Level	Turbidity (NTU)			Dissolved Oxygen (DO) (mg/L)			Suspended Solid (SS) (mg/L)		
				1	2	Ave.	1	2	Ave.	1	2	Ave.
01/06/17	09:50-10:00	Fine	Mid-Depth	13.2	12.7	13.0	2.69	2.67	2.68	<2.5	<2.5	<2.5
03/06/17	17:30-17:44	Fine	Mid-Depth	13.2	12.7	13.0	2.05	2.08	2.07	11.0	11.0	11.0
06/06/17	12:30-12:45	Fine	Mid-Depth	14.5	13.9	14.2	2.83	2.67	2.75	14.0	13.0	13.5
08/06/17	08:59-09:10	Fine	Mid-Depth	11.9	12.3	12.1	2.98	2.97	2.98	5.0	5.6	5.3
10/06/17	11:05-11:14	Fine	Mid-Depth	11.2	10.6	10.9	2.87	2.86	2.87	<2.5	<2.5	<2.5
13/06/17	11:38-11:49	Cloudy	Mid-Depth	18.4	18.1	18.3	2.81	2.85	2.83	140.0	140.0	140.0
15/06/17	18:00-18:12	Cloudy	Mid-Depth	13.3	13.0	13.2	2.74	2.70	2.72	5.2	5.6	5.4
17/06/17	11:05-11:14	Cloudy	Mid-Depth	9.0	9.0	9.0	2.60	2.63	2.62	2.3	2.2	2.3
20/06/17	10:20-10:35	Cloudy	Mid-Depth	18.8	18.5	18.7	2.10	2.07	2.09	12.0	12.0	12.0
22/06/17	14:48-14:59	Cloudy	Mid-Depth	11.7	11.1	11.4	2.34	2.32	2.33	5.0	2.0	3.5
24/06/17	10:25-10:35	Fine	Mid-Depth	10.1	10.5	10.3	2.53	2.50	2.52	12.0	13.0	12.5
26/06/17	10:30-10:50	Cloudy	Mid-Depth	9.5	9.5	9.5	2.11	2.14	2.13	14.0	12.0	13.0
28/06/17	18:25-18:34	Cloudy	Mid-Depth	13.3	13.1	13.2	2.56	2.53	2.55	3.6	1.6	2.6
30/06/17	13:30-13:45	Fine	Mid-Depth	11.6	12.3	12.0	2.49	2.47	2.48	2.5	6.7	4.6
				Min		9.0	Min		2.05	Min		1.6
				Max		18.8	Max		2.98	Max		140.0
				Average		12.7	Average		2.54	Average		18.8

Remark: According to our procedure accredited by HOKLAS, the reporting limit of suspended solid is 0.5mg/L for 2L water. The reporting limit is inversely proportional to the volume of water samples used. For the suspended solid analysed on 01 June 2017 and 10 June 2017, 400mL was used and thus the reporting limit is 2.5mg/L. In 17 June 2017, 500ml water was used for suspended solid analysis and thus the reporting limit is 2.0mg/L. Therefore, suspended solid can be reported lower than 2.5mg/L.


Appendix F3

Graphical Plots of Impact Water Quality Monitoring Data


Impact Turbidity Result

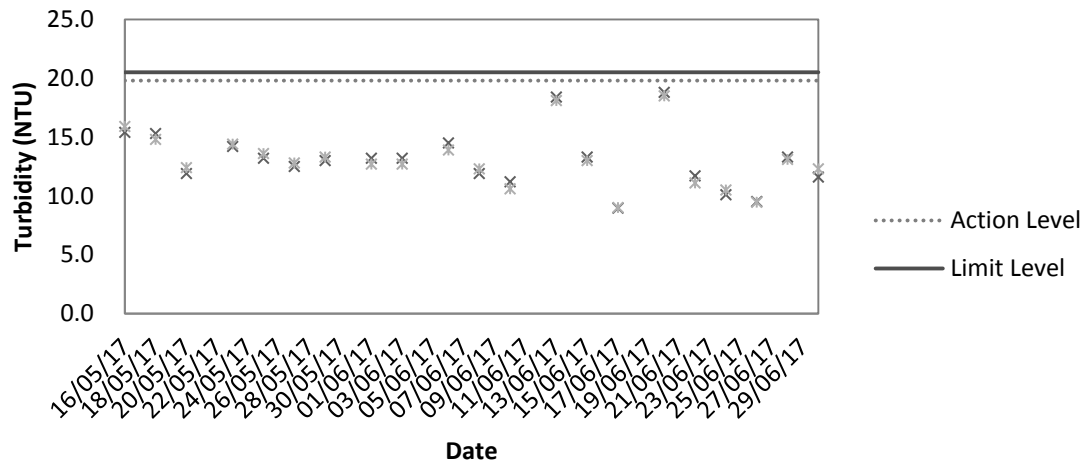

Impact Dissolved Oxygen (DO) Result

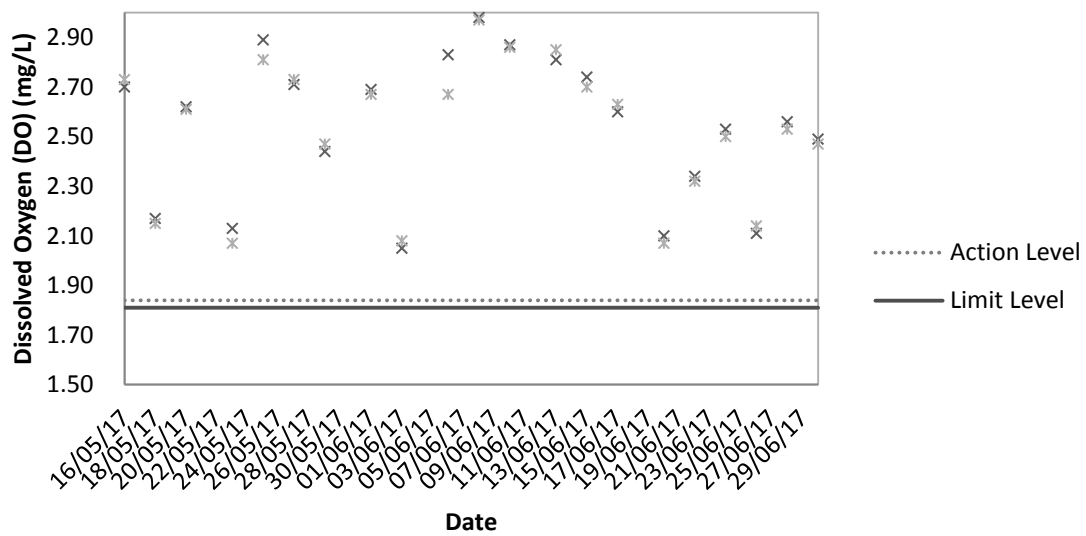

Impact Suspended Solid (SS) Result

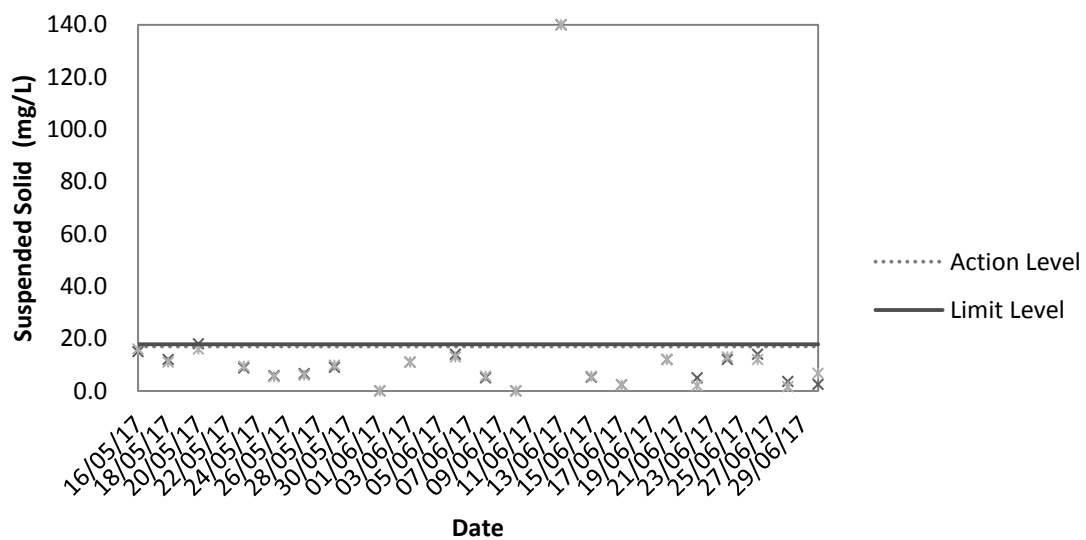

Appendix G

Weather Condition

Daily Extract of Meteorological Observations, June 2017 – Wetland Park

Day	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Total Rainfall (mm)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)					
01	1002.8	32.2	29.7	27.5	25.7	79	0.0	190	9.5
02	1002.0	32.1	30.1	28.7	26.2	80	0.0	190	8.8
03	1002.1	34.7	30.9	28.8	25.9	76	0.0	190	8.6
04	1003.1	32.8	30.0	28.4	26.5	82	0.0	150	8.3
05	1005.7	33.3	30.2	28.5	26.0	79	0.0	150	12.4
06	1008.7	33.9	30.3	27.8	25.3	75	0.0	160	9.5
07	1009.6	33.6	30.0	26.5	25.3	77	8.0	170	8.0
08	1009.5	34.0	30.0	26.5	24.7	75	0.0	170	6.8
09	1008.8	34.2	29.9	26.6	24.5	73	0.0	170	7.3
10	1007.9	33.7	30.1	27.5	24.9	74	0.0	150	7.8
11	1006.6	34.9	29.9	26.8	25.3	77	0.0	160	5.5
12	1002.5	30.5	27.6	25.6	25.2	87	23.0	090	10.0
13	1005.8	28.2	26.5	24.3	25.2	93	146.0	160	5.8
14	1008.4	29.4	27.2	25.1	25.8	92	19.5	150	2.7
15	1007.2	31.4	29.1	26.6	25.7	82	2.0	160	6.5
16	1004.8	31.1	29.1	25.4	26.0	83	9.0	180	6.6
17	1003.5	26.4	25.3	24.5	24.6	96	113.5	160	2.6
18	1004.4	28.2	26.3	24.5	24.9	92	12.0	150	3.4
19	1004.9	29.8	26.4	25.1	24.9	92	13.5	160	3.8
20	1004.8	28.3	26.1	24.8	25.0	93	21.5	160	3.7
21	1004.9	31.0#	27.5	25.2#	25.7	90	10.0	150	4.7
22	1007.4	32.4	29.3	27.6	25.5#	79#	0.0	150	8.9
23	1007.3	31.8	29.0	26.9	***	***	1.5	150	9.3
24	1005.9	31.9	28.7	26.7	***	***	1.5	150	6.4
25	1006.5	32.2	29.3	26.4	***	***	0.5	150	7.3
26	1008.0	32.8	30.0	27.4	24.9#	72#	0.0	190	8.3
27	1009.1	32.8	29.8	27.7	25.0	76	0.0	190	6.7
28	1009.8	33.1	29.9	27.2	24.1	73	0.0	140	8.0
29	1009.3	33.2	29.3	26.3	25.1	79	0.0	150	5.8
30	1007.4	33.4	29.4	25.4	24.3	75	0.0	170	6.8

*** unavailable

data incomplete

Rainfall measured in increment of 0.5 mm. Amount of < 0.5 mm cannot be detected

Appendix H

Environmental Site Inspection Checklist



Environmental Site Inspection Checklist – San Wai

Inspection Date: 2-6-17 Inspected By: Frankie Tang
Time: 14:00 Weather Condition: Fine
Participants: T.Y. Lau, Cherry Ye, Man Guanghua

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <u>not observed</u>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding $\geq 2.4\text{m}$ tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?				
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	item 1
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	item 2
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit: Follow up action to item on 26.5.17, All item was improved.

Observations

1. Stagnant Pool was observed in the hole on the ground ~~near~~^{at} near sediment tank
2. Chemical container was observed without labeled.

Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

1. The contractor should be clean the stagnant pool properly to prevent mosquito.
2. Chemical container label should be display properly.

Inspected by

Signature:

Name: Frankie Tung

Title: E.T

Date: 26.17

Checked and Approved by

Signature:

Name: C. L. Han

Title: E.T. Leader

Date: 3.6.2017

Reviewed by

Signature:

Name: T. Y. LOU

Title: ARE



Date: 3/6/2017


Name: C. Y. HING

Title: CRE

Date: 3/6/2017

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 26/05/2017, stagnant pool was cleared inside the drip trays.</p>	--	170602_001	No	--
1	 <p>Stagnant pool was observed in the hole on the ground near sediment tank.</p>	To clear the stagnant pool near sediment tank	170602_002	Yes	09/06/2017

2	 <p>Chemical container without label was observed.</p>	To display correct label on the chemical container.	170602_003	Yes	09/06/2017
---	-----------------------------------------------------------------------------------------------------------------------------------------	-----------------------------------------------------	------------	-----	------------



Environmental Site Inspection Checklist – San Wai

Inspection Date: 9 June 2017 Inspected By: Ivy Lo
Time: 09:30 Weather Condition: Sunny
Participants: C.Y. Hung, Teddy Yuen, T.Y. Lo, Johnny So, Cherry Ye

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input checked="" type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input type="checkbox"/> Others:				
2.5	Are the work sites wetted with water twice a day?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<u>Reminder 1</u>
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding $\geq 2.4\text{m}$ tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Reminder 1
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?				
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				
4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit: *Follow up action to the items on 2/6/2017, all items were improved.*


Observations *No items were observed.*

~~Reminder~~ *SM*


Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

Reminder 1. The contractor was reminded to increase the frequency of watering in order to prevent dust generation.


Inspected by
Signature:


Name: *Ivy Lo*
Title: *E.T.*
Date: *9/6/2017*



Checked and Approved by
Signature:


Name: *C. L. Lam*
Title: *E.T. Leader*
Date: *10/06/2017*

Reviewed by
Signature:


Name: *Patrick Leung*
Title: *RE*
Date: *16/6/2017*

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 02/06/2017, stagnant pool near sediment tank was cleared.</p>	--	170609_001	No	--
--	 <p>Follow up action to Item 2 on 02/06/2017, correct label was displayed on the chemical container.</p>	--	170609_002	No	--

Environmental Site Inspection Checklist – San Wai

Inspection Date: 16.6.17 Inspected By: Frankie Tong
Time: 14.00 Weather Condition: Cloudy
Participants: Patrick Leung, T.Y. Lam, Johnny So, Cherry Ye

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input checked="" type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input type="checkbox"/> Others:				
2.5	Are the work sites wetted with water twice a day?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding \geq 2.4m tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?				
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5	Waste / Chemical Management	N/A	Yes	No	Remarks
	General Waste				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
	Construction Waste				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit: N/A


Observations

No item were observed.

Corrective Actions – Mitigation Measures Implemented or Proposed (if any): N/A

Inspected by

Signature:


Name: Frankie Tong

Title: E.T

Date: 16.6.17

Checked and Approved by

Signature:



Name: C. L. Lau

Title: E.T. Leader

Date: 17.6.17

Reviewed by

Signature:


Name: C. F. Wong

Title: IOW

Date: 17.06.2017

**Environmental Site Inspection Checklist – San Wai****Inspection Date:**

23.6.17

Inspected By:

Frankie Tung

Time:

10:00

Weather Condition:

Fine

Participants:

T.Y. Lam, Johnny So, Cherry Ho, etc.

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input checked="" type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input type="checkbox"/> Others:				
2.5	Are the work sites wetted with water twice a day?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding ≥ 2.4 m tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?				
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5	Waste / Chemical Management	N/A	Yes	No	Remarks
	General Waste				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	Construction Waste				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus insert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	item 1
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

**Follow up actions for pervious Site Audit: N/A**

Observations Item 1: Oil stain was observed on the ground at Portion P1.

Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

Item 1: To clean the oil stain and treat the contaminated materials as chemical waste.

Inspected by

Signature:

Name: Frankie Tang

Title: E.T

Date: 23.6.17

Checked and Approved by

Signature:

Name: C. L. Lau

Title: E.T. Leader

Date: 24.6.17

Reviewed by


Signature:

Name: Patrick Leung

Title: Resident Engineer

Date: 30/6/2017

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
1	 <p>Oil Stain was observed on the ground at Portion P1.</p>	To clean the oil stain and treat the contaminated materials as chemical waste.	170623_001	Yes	30/06/2017



Environmental Site Inspection Checklist – San Wai

Inspection Date: 30.6.17 Inspected By: Frankie Tung
 Time: 14:00 Weather Condition: Fine
 Participants: Patrick Lam, TY Lam, Johnny So, Cherry Ye

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input checked="" type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input type="checkbox"/> Others:				
2.5	Are the work sites wetted with water twice a day?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<u>Item 1</u>
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding $\geq 2.4\text{m}$ tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	item 1
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?				
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

Follow up actions for pervious Site Audit: Follow up action to item I on 23-6-17, oil stain was cleared.


Observations Item I: Are designated road should be keep wetted to avoid dust generation.

Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

Item I: Increase the frequency of watering to control dust emission.

Inspected by

Signature:



Name: E.T. Leader

Title: E.T.

Date: 30.6.17

Checked and Approved by

Signature:



Name: C.L. Lau

Title: E.T. Leader

Date: 03.07.2017

Reviewed by



Signature:


Name: Patrick Leung

Title: RE

Date: 7/7/2017

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 23/06/2017, oil stains were cleaned.</p>	--	170630_001	No	--
1	 <p>Insufficient watering was observed</p>	To increase the frequency of watering to control dust generation.	170630_002	Yes	07/07/2017

Appendix I

Waste Flow Table

DSD Contract: DC/2013/10
Design, Build and Operate
San Wai Sewage Treatment Works Phase 1



ATAL-Degremont-China Harbour Joint Venture

Name of Department: DSD

Year: 2017

Project: Design, Build and Operate San Wai Sewage Treatment Works - Phase 1

Contract No.: DC/2013/10

Waste Flow Table

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Broken Concrete (see Note ³)	Reused in the Contract	Reused in other Projects	Disposed as Public Fill (see Note ⁴)	Imported Fill	Metals	Paper/ cardboard packaging	Plastics (see Note ³)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 kg)
Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	19.480
Feb	0.005	0.000	0.000	0.000	0.005	0.000	0.000	0.000	0.000	0.000	6.830
Mar	0.000	0.000	0.000	0.000	0.000	1.074	0.000	0.000	0.000	0.000	5.830
Apr	0.248	0.000	0.000	0.000	0.248	0.000	0.000	0.000	0.000	0.000	23.350
May	1.762	0.000	0.000	0.000	1.762	0.000	0.000	0.000	0.000	0.000	1.540
Jun	2.041	0.000	0.000	0.000	2.041	0.030	0.000	0.057	0.000	0.000	12.300
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	4.056	0.000	0.000	0.000	4.056	1.104	0.000	0.057	0.000	0.000	69.330

Notes: (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.

(2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.

(3) Broken concrete for recycling into aggregates.

(4) Assumption: The densities of subbase, Rockfill, Soil, Mix Rock and Soil, Reclaimed Asphalt Pave, Slurry are 2.0 ton/m³; the densities of Building debris is 2.1 ton/m³; the densities of Broken Concrete is 2.4 ton/m³.

Appendix J

Environmental Licenses and Permits

Item No.	Nature of Permit / License / Notification	Permit / License /Notification No.	Date of Issue / Effective of Permit / License	Date of Expiry of Permit / License	Remark (Validity for reporting period only)
1	Environmental Permit	EP-464/2013	18/10/2013	NA	Valid
2	Billing Account for Disposal of Construction Waste	7025330	07/07/2016	NA	Valid
3	Form NA notification (for APCO)	405489	26/07/2016	25/09/2020	Valid
4	Construction Noise Permit (for Site)	GW-RN0060-17	30/01/2017	12/06/2017	Expired
5	Chemical Waste Producer Registration (for Site)	5218-511-A2823-01	23/01/2017	NA	Valid
6	Wastewater Discharge Licence (for WPCO)	WT00026754-2017	28/04/2017	31/01/2022	Valid
7	Construction Noise Permit (for piling works)	PP-RN0010-17	01/04/2017	30/06/2017	Expired
8	Construction Noise Permit (for Site)	GW-RN0420-17	25/06/2017	12/12/2017	Valid
9	Construction Noise Permit (for pilling works)	PP-RN0030-17	03/07/2017	30/12/2017	Valid

Appendix K

Implementation Schedule for Environmental Mitigation Measures (EMIS)

Environmental Mitigation Measures	Location	Implementation Status			
		Implemented	Partially implemented	Not implemented	Not Applicable
Air Quality					
<ul style="list-style-type: none">The working area for the uprooting of trees, shrubs, or vegetation or for the removal of boulders, poles, pillars or temporary or permanent structures should be sprayed with water or a dust suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;	Site Area	√			
<ul style="list-style-type: none">All demolished items (including trees, shrubs, vegetation, boulders, poles, pillars, structures, debris, rubbish and other items arising from site clearance) that may dislodge dust particles should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition;	Site Area	√			
<ul style="list-style-type: none">Vehicle washing facilities including a high pressure water jet should be provided at every discernible or designated vehicle exit point;	Site Entrance	√			
<ul style="list-style-type: none">The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;	Site Exit	√			
<ul style="list-style-type: none">Where a site boundary adjoins a road, street, service and or other area accessible to the public, hoarding of not less than 2.4m from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit;	Site Area	√			
<ul style="list-style-type: none">Every main haul road (i.e. any course inside a construction site having a vehicle passing rate of higher than 4 in any 30 minutes) should be paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical so as to maintain the entire road surface wet;	Main Haul Road	√			
<ul style="list-style-type: none">The portion of any road leading only to a construction site that is within 30m of a discernible or designated vehicle entrance or exit should be kept clear of dusty materials;	Site Entrance and Exit	√			
<ul style="list-style-type: none">Immediately before leaving a construction site, every vehicle should be washed to remove any dusty materials from its body and wheels;	Site Exit	√			
<ul style="list-style-type: none">Where a vehicle leaving a construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle;	--	√			
<ul style="list-style-type: none">The working area of any excavation or earth moving operation should be sprayed with water or a dusty suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;	Site Area	√			
<ul style="list-style-type: none">Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable	Site Area	√			

surface stabilizer within 6 months after the last construction activity on the construction site or part of the construction site where the exposed earth lies;					
<ul style="list-style-type: none"> Any stockpile of dusty material should be either covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or a dust suppression chemical so as to maintain the entire surface wet. 	Site Area	√			
Noise					
<ul style="list-style-type: none"> Quiet plants should be used in order to reduce the noise impacts to protect the nearby NSRs. 	Site Area	√			
<ul style="list-style-type: none"> Temporary and Movable Noise Barriers should be used in order to reduce the noise impact to the surrounding sensitive receivers 	Site Area	√			
<ul style="list-style-type: none"> Intermittent noisy activities should be scheduled to minimize exposure of nearby NSRs to high levels of construction noise. 	Site Area	√			
<ul style="list-style-type: none"> Idle equipment should be turned off or throttled down. 	Site Area	√			
<ul style="list-style-type: none"> Construction activities should be planned so that parallel operation of several sets of equipment close to a given receiver is avoided 	Site Area	√			
<ul style="list-style-type: none"> Construction plant should be properly maintained and operated. 	Site Area	√			
Water Quality					
<ul style="list-style-type: none"> Exposed stockpiles should be covered with tarpaulin or impervious sheets before a rainstorm occurs; 	Site Area	√			
<ul style="list-style-type: none"> The exposed soil surfaces should also be properly protected to minimize dust emission; 	Site Area	√			
<ul style="list-style-type: none"> The stockpiles of materials should be placed in the locations away from the drainage channel so as to avoid releasing materials into the channel; 	Site Area	√			
<ul style="list-style-type: none"> Wheel washing facilities should be provided at site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles; 	Site Exit	√			
<ul style="list-style-type: none"> Provision of site drainage systems and treatment facilities would be required to minimize the water pollution; 	Site Area	√			
<ul style="list-style-type: none"> A discharge license needs to be applied from EPD for discharging effluent from the construction site; 	--	√			
<ul style="list-style-type: none"> The treated effluent quality is required to meet the requirements specified in the discharge license; 	--	√			
<ul style="list-style-type: none"> Provision of chemical toilets is required to collect sewage from workforce. The chemical toilets should be cleaned on a regular basis; 	Chemical Toilet	√			

<ul style="list-style-type: none"> A licensed waste collector should be employed to clean the chemical toilets and temporary storage tank on a regular basis; 	--	√			
<ul style="list-style-type: none"> Illegal disposal of chemicals should be strictly prohibited; 	Site Area	√			
<ul style="list-style-type: none"> Registration as a chemical waste producer is required if chemical wastes are generated and need to be disposed of. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes; 	Site Area	√			
<ul style="list-style-type: none"> Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance should be used as a guideline for handling chemical wastes; 	Site Area	√			
<ul style="list-style-type: none"> The impact from accidental spillage of chemicals can be effectively controlled through good management practices. 	Site Area	√			
Waste Management					
<ul style="list-style-type: none"> Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; 	Site Area	√			
<ul style="list-style-type: none"> To encourage collection of aluminium cans by individual collectors, separate bins should be provided to segregate this waste from other general refuse generated by the workforce; 	Site Area	√			
<ul style="list-style-type: none"> Any unused chemicals or those with remaining functional capacity should be recycled; 	Site Area	√			
<ul style="list-style-type: none"> Prior to disposal of C&D waste, it is recommended that wood, steel and other metals be separated for re-use and/or recycling and inert waste as fill material to minimize the quantity of waste to be disposed of to landfill; 	Site Area	√			
<ul style="list-style-type: none"> Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and 	Site Area	√			
<ul style="list-style-type: none"> Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste. 	Site Area	√			

Appendix L

Environmental Site Inspection Schedule

**Contract No. DC/2013/10 -
Design, Build and Operate San Wai Sewage Treatment Works – Stage 1
Schedule for Environmental Monitoring and Site Inspection**

June 2017

Sun	Mon	Tue	Wed	Thu	Fri	Sat
				1 WQM	2 SI	3 WQM
4	5	6 24hr-TSP 1hr-TSP x 3 NM WQM	7	8 WQM	9 SI	10 WQM
11	12 24hr-TSP 1hr-TSP x 3 NM	13 WQM	14	15 WQM	16 SI	17 24hr-TSP 1hr-TSP x 3 NM WQM
18	19	20 WQM	21	22 WQM	23 24hr-TSP 1hr-TSP x 3 NM SI	24 WQM
25	26 WQM	27	28 WQM	29 24hr-TSP 1hr-TSP x 3 NM	30 WQM SI	

**Contract No. DC/2013/10 -
Design, Build and Operate San Wai Sewage Treatment Works – Stage 1
Schedule for Environmental Monitoring and Site Inspection**

July 2017

Sun	Mon	Tue	Wed	Thu	Fri	Sat
						1
2	3	4 WQM	5 24hr-TSP 1hr-TSP x 3 NM	6 WQM	7 SI	8 WQM
9	10	11 24hr-TSP 1hr-TSP x 3 NM WQM	12	13 WQM	14 SI	15 WQM
16	17 24hr-TSP 1hr-TSP x 3 NM	18 WQM	19	20 WQM	21 SI	22 24hr-TSP 1hr-TSP x 3 NM WQM
23	24	25 WQM	26	27 WQM	28 24hr-TSP 1hr-TSP x 3 NM SI	29 WQM
30	31					

Appendix M

Investigation Reports on Action Level or Limit Level Non-compliance

Report No. 001
Monitoring Date 13 June 2017

The Action and Limit Levels of suspended solids (SS) determined from baseline monitoring data are reproduced below:

Monitoring Parameter	Action Level (AL)	Limit Level (LL)
Suspended Solid (mg/L)	17.0	17.8

Suspended Solid (in mg/L)

Monitoring Station	Monitoring Duration	Result			Level Exceedance
		Trial 1	Trial 2	Average	
R1b	11:38 to 11:49	140	140	140	Limit

Investigation Results:

a) Causes of exceedances

Exceedance was not due to construction works under Contract No. DC/2013/10 because:

- Tropical Cyclone Warning Signal No.8 was hoisted from 12 to 13 June 2017. The soil and other suspended materials were flushed along the shore and entered the Tin Shui Wai Nullah. Therefore, the water quality at R1b was deteriorated and resulted in suspended solids exceedance.
- Red Rainstorm Warning Signal was hoisted during water monitoring period on 13 June 2017. The nullah water was thus flowed rapidly and the sand and stones in the nullah bed were upturned. Thus, the water quality at R1b was deteriorated and resulted in suspended solids exceedance.
- During the above mentioned bad weather on 12 and 13 June 2017, all works were suspended and workers were off-site from 12:00noon 12 June 2017 to 1:30pm 13 June 2017 due to occurrence of the tropical storm, Merbok.
- Besides, a temporary storage pool was established in the lowest position of the construction site for acting as a prior sedimentation tank. Indeed, the surface runoff was first stored in the temporary storage pool and then transferred to the Wetsep for proper treatment prior to discharge. The effluent was thus brought into an acceptable minimum level and also complied with the requirements specified in the discharge license. In addition, there was no water discharge in the morning of 13 June 2017.
- Thus, the exceedance of water samples taken from 11:38 to 11:49am on 13 June 2017 was considered as non-Project related.

Investigation Report on Action Level or Limit Level Non-compliance

b) Action required under the action plan

Refer to Table 4.4 of the EM&A Manual.

c) Action taken under the action plan

1. Not applicable as suspended solids was not measured in-situ;
2. After considered the above mentioned investigation results, it appears that it was unlikely that the suspended solids exceedance was attributed to the work site of this Contract;
3. The exceedance was informed to IEC and Contractors;
4. Monitoring data, all plant, equipment and Contractor's working methods were checked;
5. Mitigation measures and recommendations were provided in item d).
6. Mitigation measures implementation status were shown in the attachment.
7. The water quality monitoring results of 15 June 2017 was shown below:

Test Parameters	Trial 1	Trial 2	Average	Action Level	Limit Level
Turbidity (NTU)	13.3	13.0	13.2	19.8	20.5
Dissolved Oxygen (mg/L)	2.74	2.70	2.72	1.84	1.81
Suspended Solid (mg/L)	5.2	5.6	5.4	17.0	17.8

The results of suspended solid of the water samples collected on 15 June 2017 were under the action limit.

d) ET's conclusions and recommendations for mitigation

- All relevant water quality mitigation measures were checked to be fully implemented including provision of site drainage systems and treatment facilities, maintaining the existing silt trap to ensure good efficiency of wheel wash facilities, complying the requirements specified in the discharge license. The effluent quality report was shown in **Appendix A**. According to the photos below, water overflowed from the discharge point is clean without mud





Investigation Report on Action Level or Limit Level Non-compliance

- The Contractor was reminded to ensure all construction activities that generate wastewater with high concentrations of suspended solids (SS) should be collected to sedimentation tanks or package treatment systems for proper treatment prior to discharge.
- e) Contractor's actions to implement the mitigation
- All construction activities that generate wastewater with high concentrations of suspended solids (SS) like wheel washing etc. was collected to sedimentation tanks or package treatment systems for proper treatment prior to discharge.
 - All silt removal facilities, channels and manholes was maintained and any deposited silt and grit was removed regularly.

Prepared by:



LO, Ting Yi


Certified by:



LAU, Chi Leung
Environmental Team Leader

Appendix N

Laboratory Report for Discharge Water



TEST REPORT

Environmental Testing of Water & Wastewater

Superseding test report no. ENA73660

Report No. : ENA73660A

Date of issue : 02 August 2017

Page No. : 1 of 1

Information provided by Customer

Customer name : ATAL - Degremont - China Harbour Joint Venture
Customer address : 19/F, China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of sampling : 10 June 2017
Sample Description : The sample was collected by the Customer.
The sample was stored in 1L plastic bottle (for pH) and
500ml plastic bottle (for Chemical Oxygen Demand). The sample was chilled when received.
Sample for Chemical Oxygen Demand was preserved by adding conc H₂SO₄ to pH<2.

Laboratory information

Date Received : 10 June 2017

Result

Customer Sample ID	Lab Ref No	Test	Method Used	Result	Date Tested
DC201310-T01	W39102 (01)	pH	In house method TPE/003/W	7.8 (at 25°C)	10 June 2017
	W39102 (03)	Chemical Oxygen Demand	In house method TPE/002/W	43 mgO ₂ /L	12 June 2017

Remark (if any) : -

Checked by :


LAW, Sau Yee
(Senior Chemist)

Approved Signatory :

LAU, Chi Leung

This report shall not be reproduced unless with prior written approval from this laboratory.

-END OF REPORT-



東業德勤測試顧問有限公司
ETS-TESTCONSULT LTD.

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: etl@ets-testconsult.com
W: www.ets-testconsult.com

TEST REPORT

Environmental Testing of Water & Wastewater

Report No. : ENA73661
Date of issue : 17 June 2017
Page No. : 1 of 1

Information provided by Customer

Customer name : China Harbour Engineering Co Ltd
Customer address : 19/F, China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of sampling : 10 June 2017
Sample Description : The sample was collected by the Customer.
The sample was stored in 1L plastic bottle (Total Suspended Solids) and
The sample was chilled when received.

Laboratory information


Date Received : 10 June 2017

Result


Customer Sample ID	Lab Ref No	Test	Method Used	Result	Date Tested
DC201310-T02	W39102 (02)	Total Suspended Solids	In house method TPE/006/W	17 mg/L *	15 June 2017

Remark (if any) : (*) 200ml sample was used for Total Suspended Solids analysis. PQL of Total Suspended Solids reported less than 5 mg/L.

Checked by :


LAW, Sau Yee
(Senior Chemist)

Approved Signatory :


LAU, Chi Leung

This report shall not be reproduced unless with prior written approval from this laboratory.

-END OF REPORT-



東業德勤測試顧問有限公司 ETS-TESTCONSULT LTD.™

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pul Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: etl@ets-testconsult.com
W: www.ets-testconsult.com

TEST REPORT

Environmental Testing of Water & Wastewater

Report No. : ENA73983
Date of issue : 30 June 2017
Page No. : 1 of 1

Information provided by Customer

Customer name : ATAL - Degremont - China Harbour Joint Venture
Customer address : 19/F China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of sampling : 20 June 2017
Sample Description : The sample was collected by the Customer.
The sample was stored in 1L plastic bottle.

Laboratory information


Date Received : 23 June 2017

Result

Customer Sample ID	Lab Ref No	Test	Method Used	Result	Date Tested
DC201310-001	W39223 (01)	Total Suspended Solids	In house method TPE/006/W	11 mg/L *	27 June 2017

Remark (if any) : (*) 500ml sample was used for Total Suspended Solids analysis. PQL of Total Suspended Solids reported less than 2 mg/L.

Checked by :


LAW, Sau Yee
(Senior Chemist)

Approved Signatory :


LAU, Chi Leung

This report shall not be reproduced unless with prior written approval from this laboratory.

-END OF REPORT-



TEST REPORT

Environmental Testing of Water & Wastewater

Report No. : ENA74783
Date of issue : 07 August 2017
Page No. : 1 of 1

Information provided by Customer

Customer name : ATAL - Degremont - China Harbour Joint Venture
Customer address : 19/F China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of sampling : 30 June 2017
Sample Description : The sample was collected by the Customer.
The sample was stored in 1L plastic bottle (for pH) and
500ml plastic bottle (for Chemical Oxygen Demand). The sample was chilled when received.
Sample for Chemical Oxygen Demand was preserved by adding conc H₂SO₄ to pH<2.

Laboratory information

Date Received : 27 July 2017

Result

Customer Sample ID	Lab Ref No	Test	Method Used	Result	Date Tested
DC201310-001A	W39506 (01)	pH	In house method TPE/003/W	9.1 (at 25°C)	27 July 2017
	W39506 (02)	Chemical Oxygen Demand	In house method TPE/002/W	<10 mgO ₂ /L	31 July 2017

Remark (if any) : ---

Checked by :

LAW, Sau Yee
(Senior Chemist)

Approved Signatory :


LAU, Chi Leung

This report shall not be reproduced unless with prior written approval from this laboratory.

-END OF REPORT-

Figure 1


Locations of Air Quality and Noise Monitoring Stations

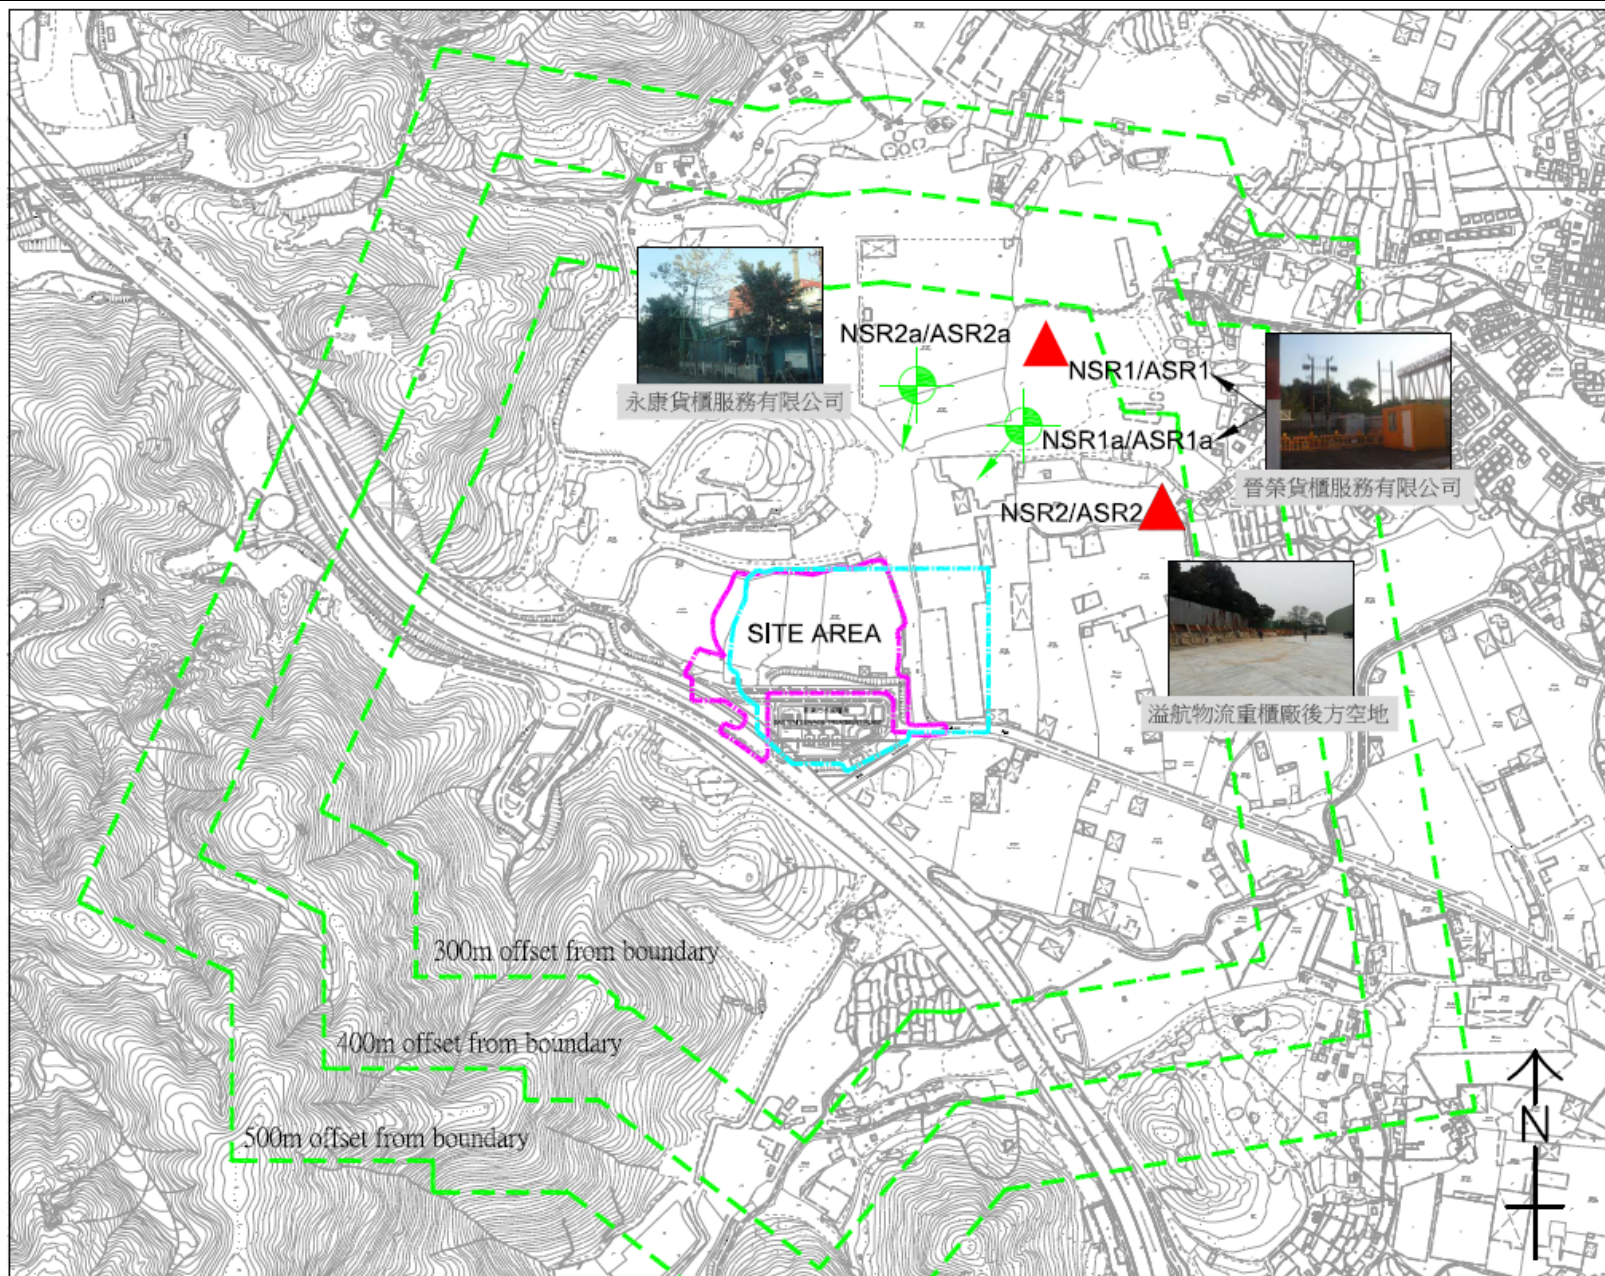

Project: Contract No. DC/2013/10 -Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Figure 1 Locations of Air Quality and Noise Monitoring Stations

Figure 2

Locations of Water Quality Monitoring Station

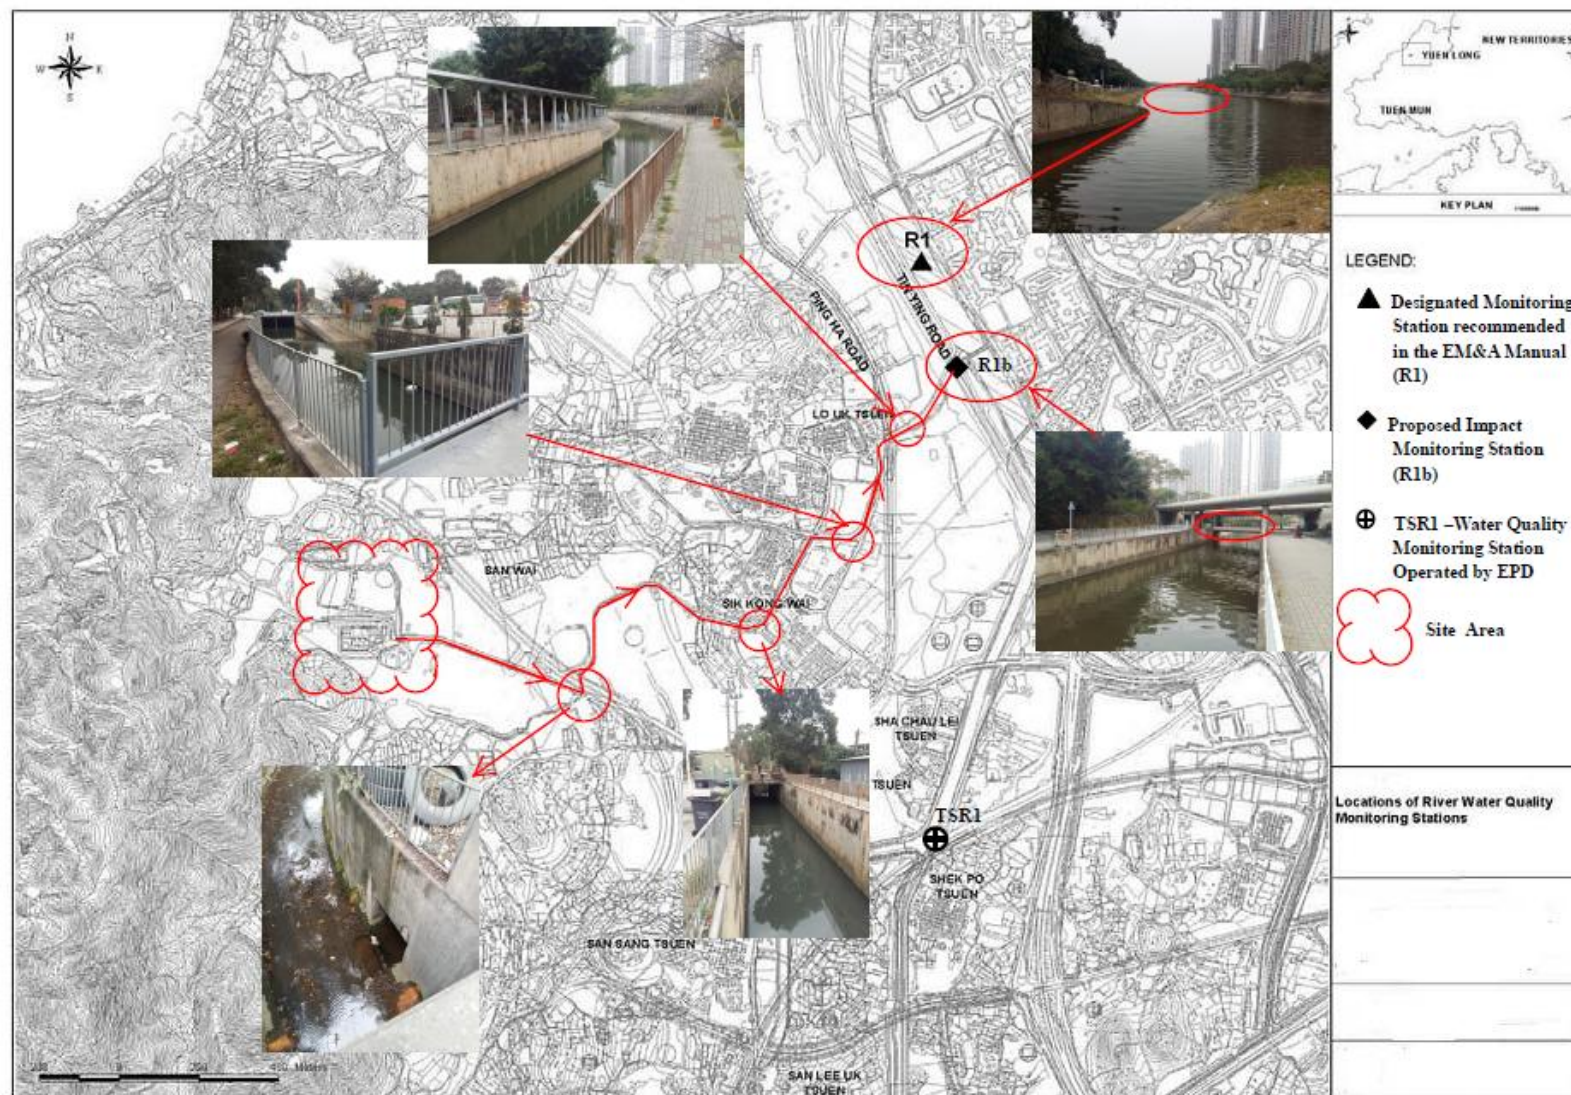

Project: Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Figure 2 Locations of Water Quality Monitoring Station
