



東業德勤測試顧問有限公司
ETS-TESTCONSULT LTD.TM

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: eti@ets-testconsult.com
W: www.ets-testconsult.com



ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE

**CONTRACT NO. DC/2013/10 - DESIGN,
BUILD AND OPERATE SAN WAI
SEWAGE TREATMENT WORKS –
PHASE 1**

**MONTHLY EM&A REPORT
NO. 21**

(01 JANUARY – 31 JANUARY 2019)

Prepared by:


LO, Ting Yi

Certified by:


LAU, Chi Leung
Environmental Team Leader

Issued Date: 13 February 2019

Report No.: ENA91131

This report shall not be reproduced unless with prior written approval from this laboratory.



Drainage Services Department
Sewage Services Branch
Harbour Area Treatment Scheme
5/F, Western Magistracy
2A Po Fu Lam Road
Hong Kong

Your reference:

Our reference: HKDSD203/50/105549

Date: 18 February 2019

Attention: Mr Albert Wong

BY EMAIL & POST
(email: awong@dsd.gov.hk)

Dear Sirs

Agreement No. HATS 02/2016
Services for Independent Environmental Checker (IEC) for
Contract No. DC/2013/10 – Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Monthly Environmental Monitoring and Audit Report No.21 (January 2019)

We refer to emails of 13 and 16 February 2019 from ETS-Testconsult Limited attaching the Monthly Environmental Monitoring and Audit Report No.21 (January 2019).

We have no comment and hereby verify the Monthly Environmental Monitoring and Audit Report No.20 (December 2018) in accordance with Clause 5.4 of the Environmental Permit no. EP-464/2013.

Should you have any queries, please do not hesitate to contact the undersigned or our Mr Nic Lam on 2618 2831.

Yours faithfully
ANewR CONSULTING LIMITED

Adil Uee
Independent Environmental Checker

LYMA/LHHN/LCCR/lhnh

cc AECOM – Mr Patrick Leung (email: patrick.leung@swstw-aecom.com)
ETS-Testconsult Limited – Mr C L Lau (email: env@ets-testconsult.com)



TABLE OF CONTENTS

EXECUTIVE SUMMARY

1	INTRODUCTION	1-2
1.1	Basic Project Information	1
1.2	Project Organization	1-2
1.3	Construction Programme	2
1.4	Construction Works Undertaken During the Reporting Period	2
2	AIR QUALITY MONITORING	3-7
2.1	Monitoring Requirements	3
2.2	Monitoring Equipment	3-4
2.3	Monitoring Parameters, Frequency and Duration	4
2.4	Action and Limit Levels	5
2.5	Results and Observations	5
2.6	Event and Action Plan	5-7
3	NOISE MONITORING	8-11
3.1	Monitoring Requirements	8
3.2	Monitoring Equipment	8
3.3	Monitoring Duration and Frequency	8
3.4	Monitoring Locations	8
3.5	Monitoring Methodology	9
3.6	Actions and Limit Level	9
3.7	Results and Observation	9
3.8	Event and Action Plan	9-11
4	WATER QUALITY MONITORING	11-16
4.1	Monitoring Requirements	11
4.2	Monitoring Methodology and Equipment	11
4.3	Monitoring Frequency	12
4.4	Quality Assurance (QA) / Quality Control (QC)	12
4.5	Action and Limit Levels	12-13
4.6	Result and Observation	13
4.7	Event and Action Plan	13-16
5	ENVIRONMENTAL SITE INSPECTION AND AUDIT	16-20
5.1	Site Inspection	16
5.2	Landscape and Visual Audit	17
5.3	Advice on the Solid and Liquid Waste Management Status	17
5.4	Discharge License and Results of Effluent Monitoring	17-18
5.5	Environmental Licenses and Permits	18
5.6	Implementation Status of Environmental Mitigation Measures	18-19
5.7	Summary of Exceedance of the Environmental Quality Performance Limit	19-20
5.8	Summary of Complaints, Notification of Summons and Successful Prosecution	20
6	FUTURE KEY ISSUES	20-22
6.1	Construction Programme for the Coming Months	20
6.2	Key Issues for the Coming Month	20-21
6.3	Environmental Monitoring and Site Inspection Schedule for the Coming Month	21
7	CONCLUSION	21
7.1	Conclusion	21

LIST OF TABLES

Table 1.1	Contact Information of Key Personnel
Table 2.1	Air Quality Monitoring Equipment
Table 2.2	Monitoring Parameters, Duration and Frequencies of Impact Air Quality Monitoring
Table 2.3	Time Schedule of Impact Air Quality Monitoring
Table 2.4	The criteria of Action and Limit Levels for Air Quality
Table 2.5	Action and Limit Levels for 1-hour TSP and 24-hour TSP
Table 2.6	Event and Action Plan for Air Quality (Dust) during Construction Phase
Table 3.1	Noise Monitoring Equipment
Table 3.2	Time Schedule of Impact Noise Monitoring
Table 3.3	Noise Monitoring Stations
Table 3.4	Action and Limit Levels for Noise Monitoring
Table 3.5	Event/Action Plan for Construction Noise
Table 4.1	Summary of Testing Procedures for water samples
Table 4.2	Monitoring Frequency of Water Quality Monitoring
Table 4.3	Time Schedule of Impact Water Quality Monitoring
Table 4.4	The criteria of Action and Limit Levels for Water Quality
Table 4.5	Action and Limit Levels for Water Quality
Table 4.6	Event and Action Plan for Water Quality
Table 5.1	Summary of Observation of site inspections
Table 5.2	Summary of Quantities of Inert C&D Materials
Table 5.3	Summary of Quantities of C&D Materials
Table 5.4	Summary of Environmental Complaints Notification of Summons and Successful Prosecution

LIST OF APPENDICES

Appendix A	Location of Work Area
Appendix B	Project Organization Chart
Appendix C	Construction Programme
Appendix D1	Calibration Certificates for Impact Air Quality Monitoring Equipment
Appendix D2	Impact Air Quality Monitoring Results
Appendix D3	Graphical Plots of Impact Air Quality Monitoring Results
Appendix E1	Calibration Certificates for Impact Noise Monitoring Equipment
Appendix E2	Impact Noise Monitoring Results
Appendix E3	Graphical Plots of Impact Noise Monitoring Data
Appendix F1	Calibration Certificates for Impact Water Quality Monitoring Equipments
Appendix F2	Impact Water Quality Monitoring Results
Appendix F3	Graphical Plots of Impact Water Quality Monitoring Data
Appendix G	Weather Condition
Appendix H	Environmental Site Inspection Checklists
Appendix I	Landscape and Visual Impact Assessment Checklist
Appendix J	Waste Flow Table
Appendix K	Environmental Licenses and Permits
Appendix L	Implementation Schedule for Environmental Mitigation Measures (EMIS)
Appendix M	Environmental Site Inspection Schedule
Appendix N	Laboratory Report for Discharge Water

FIGURES

Figure 1	Air Quality and Noise Monitoring Stations
Figure 2	Water Quality Monitoring Stations
Figure 3	Location Plan for the Wetsep Treatment Tank

EXECUTIVE SUMMARY

This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Stage 1 (the Project) (hereafter referred to as “the Contract”). The Contract was awarded to ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE (ADCJV) by the Drainage Services Department (DSD) and ETS-Testconsult Limited was appointed as the Environmental Team (ET) by ADCJV to implement the EM&A program in compliance with the EP and the EM&A Manuals.

According to the Section 25 of the Particular Specification (PS) and the Environmental Permit No. EP-464/2013, an EM&A programme should be implemented in accordance with the procedures and requirements in the EM&A Manual of the approved EIA report (Registration No. AEIAR-072/2003). The scope of monitoring works includes air quality, construction noise, water quality and environmental site audit.

Baseline monitoring was completed in April 2017. Action and Limit Levels were established for air quality, noise and water quality parameters based on the baseline monitoring results.

This is the twenty-first Monthly Environmental Monitoring and Audit (EM&A) Report for the Contract which summaries findings of the EM&A works conducted during the reporting period from 01 January 2019 to 31 January 2019.

Site Activities

As informed by the Contractor, site activities were carried out in this reporting month:

- *Substructure (rc structure);*
- *Backfilling;*
- *Substructure (ELS & Bulk excavation);*
- *Superstructure (rc and metalworks);*
- *Water Tightness Test;*
- *ABWF - Sludge Dewatering Building;*
- *ABWF - Administration Building & Maintenance Workshop;*
- *Pile Loading Test;*
- *Post-Drilling;*
- *Bar Screen Installation;*
- *Slope works and Retaining Wall (Eastern Portion);*
- *Slope works and Retaining Wall (Northern Portion);*
- *CLP Cable Duct and Draw Pits (within the Site);*
- *EVA (Road & Drainage);*
- *RC Trench and Odour Pipe (DO1, DO2);*
- *Emergency By-Pass Pipe;*
- *Sewage Pipe;*
- *Cable Duct and Draw Pits*



Environmental Monitoring and Audit Progress

The monthly EM&A programme was undertaken in accordance with the EM&A Manual for this Contract. The summary of the monitoring activities in this reporting month is listed below:

- *24-hour TSP Monitoring: 5 Occasions at 2 designated locations*
- *1-hour TSP Monitoring: 15 Occasions at 2 designated locations*
- *Noise Monitoring (Day-time): 5 Occasions at 2 designated locations*
- *Water Quality Monitoring: 13 Occasions at 1 designated location*
- *Weekly Site inspection: 5 Occasions*

Air Quality Monitoring

No exceedance of Action and Limit levels was recorded for 1-hr and 24-hr TSP monitoring in the reporting month.

Noise Monitoring

No exceedance of Action and Limit levels for noise monitoring was recorded in the reporting month.

Water Quality Monitoring

According to the summary of water monitoring results, no exceedance of Action and Limit levels was recorded in this reporting month.

Weekly Site Inspections

In general, performance on environmental mitigation measures implemented was found to be satisfactory in this reporting month. The major findings observed during site inspections are presented in the **Section 5.0**.

Complaint Log

There was no complaint received in relation to the environmental impact during the reporting period.

Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during the reporting period.

Reporting Change

There were no reporting changes during the reporting period.

Future Key Issues

The future key issues to be undertaken in the upcoming month are as follows:

- *Chemical and waste management;*
- *Treatment of runoff and wastewater prior to discharge; and*
- *Dust and Noise generated from construction activities*

1. INTRODUCTION

1.1. Basic Project Information

- 1.1.1. This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Stage 1 (the Project) (hereafter referred to as “the Contract”). The Contract was awarded to ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE (ADCJV) by the Drainage Services Department (DSD) and ETS-Testconsult Limited was appointed as the Environmental Team (ET) by ADCJV to implement the EM&A program in compliance with the EP and the EM&A Manuals.
- 1.1.2. The project involves expansion of the preliminary treatment works at San Wai STW from 164,000 m³/d to 200,000 m³/d Average Dry Weather Flow, upgrading the preliminary treatment level to CEPT and adding centralized disinfection. The site layout plan is shown in **Appendix A**.
- 1.1.3. According to the Section 25 of the Particular Specification (PS) and the Environmental Permit No. EP-464/2013, an EM&A programme should be implemented by an independent Environmental Team (ET) in accordance with the procedures and requirements in the EM&A Manual of the approved EIA report (Registration No. AEIAR-072/2003). These documents are available through the EIA Ordinance Register. The construction works of the Contract commenced on 16 May 2017.
- 1.1.4. The scope of monitoring works includes air quality, construction noise, water quality and environmental site audit. The EM&A requirements for each parameter described in the following sections include:
- All monitoring parameters;
 - Monitoring schedules for the reporting month and forthcoming months;
 - Action and Limit levels for all environmental parameters;
 - Event/Action Plans;
 - Environmental mitigation measures, as recommended in the Project EIA study final report; and
 - Environmental requirements in contract documents.
- 1.1.5. As part of the project EM&A program, baseline monitoring was conducted from 21 March 2017 to 15 April 2017 to determine the ambient environmental conditions before the project commence any major construction works and it had been verified by IEC and endorsed by EPD.
- 1.1.6. This is the twenty-first Monthly Environmental Monitoring and Audit (EM&A) Report for the Contract which summaries the audit findings of the EM&A programme during the reporting period from 01 January 2019 to 31 January 2019.

1.2. Project Organization

- 1.2.1. The project organization structure and lines of communication with respect to the on-site environmental management structure is shown in **Appendix B**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name of Key Staff	Tel. No.	E-mail
Supervising Officer (AECOM Asia Co. Ltd.)	Resident Engineer	Mr. Patrick Leung	5222 6561	patrick.leung@swstw-aecom.com
Independent Environmental Checker (ANewR Consulting Limited)	Technical Director	Mr. Adi Lee	2618 2836	aymlee@anewr.com
	Senior Environmental Consultant	Mr. Nic Lam	2618 2836	nhhlam@anewr.com
Contractor (ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE)	Environmental Officer	Mr. Johnny So	9513 8899	johnny.so@c302.checkk.com
Environmental Team (ETS-Testconsult Ltd.)	Environmental Team Leader	Mr. C. L. Lau	2946 7791	env@ets-testconsult.com

1.3. Construction Programme

1.3.1. A copy of the Contractor's construction programme is provided in **Appendix C**.

1.4. Construction Works Undertaken During the Reporting Period

1.4.1. A summary of the construction activities undertaken during this reporting period is shown below:

- Substructure (rc structure);
- Backfilling;
- Substructure (ELS & Bulk excavation);
- Superstructure (rc and metalworks);
- Water Tightness Test;
- ABWF - Sludge Dewatering Building;
- ABWF - Administration Building & Maintenance Workshop;
- Pile Loading Test;
- Post-Drilling;
- Bar Screen Installation;
- Slope works and Retaining Wall (Eastern Portion);
- Slope works and Retaining Wall (Northern Portion);
- CLP Cable Duct and Draw Pits (within the Site);
- EVA (Road & Drainage);
- RC Trench and Odour Pipe (DO1, DO2);
- Emergency By-Pass Pipe;
- Sewage Pipe;
- Cable Duct and Draw Pits

2. AIR QUALITY MONITORING

2.1. Monitoring Requirements

- 2.1.1. 1-hr and 24-hr TSP levels were monitored in the reporting month in accordance with the EM&A Manual. Two air monitoring locations were selected which was shown in **Figure 1**.

2.2. Monitoring Equipment

1-hour TSP Monitoring

1-hour TSP levels were measured by using dust meter which are capable of producing comparable results as the by high volume sampling method, to indicate short event impacts. The dust meter is compliant to the clause 1.2.5 of "General Technical Requirement of Environmental Monitoring" and clause 2.2 of "Generic Environmental Monitoring and Audit Manual".

Table 2.1 summarized the dust meter model used during the baseline monitoring. Copies of calibration certificates for dust meters were attached in **Appendix D1**.

Table 2.1 Air Quality Monitoring Equipment

Equipment	Model
Dust Meter	SIBATA LD-3B / SIBATA LD-5
High volume sampler (HVS)	Greasby GMW (GS2310)
Calibrator	Tisch TE-5025A

1-hr air quality monitoring (Dust Meter)

Measuring Procedures

The measuring procedures of the dust meter are in accordance with the Manufacturer's instruction Manual as follows:

- Press POWER to ON, check the battery indicator to ensure whether the power supply is enough to conduct the TSP monitoring;
- Press TIMER SET to Manual;
- Press START/STOP SWITCH to start the TSP monitoring;
- Press START/STOP SWITCH to stop the TSP monitoring after monitoring complete;
- Record measured COUNT directly from the dust meter and calculate the TSP level by using the equation of the certificate.

Maintenance & Calibration (QA/QC)

- Dust meter should be checked at 3-month intervals and calibrated at half-year intervals throughout all stages of air quality monitoring.

24-hr air quality monitoring (HVS)

Instrumentation

High volume sampler, as HVS, (Greasby GMWS2310) complete with appropriate sampling inlets were employed for both 1-hour and 24-hour TSP monitoring. The sampler is composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complies with that required by USEPA standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

Installation

The installation of HVS refers to the requirement stated in EM&A Manual.

Operation/Analytical Procedures

Operating/analytical procedures for the operation of HVS are as below:

- Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 0.6m³/min and 1.7m³/min.) in accordance with the manufacturer's

instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50. The flow rate was indicated on the flow rate chart.

- For TSP sampling, fiberglass filters (Whatman G653) were used.
- The power supply was checked to ensure the sampler worked properly.
- On sampling, the sampler was operated 5 minutes to establish thermal equilibrium before placing any filter media at designated air monitoring station.
- The filter holding frame was then removed by loosening the four nuts and carefully a weighted and conditioned filter was centered with the stamped number upwards, on a supporting screen.
- The filter was aligned on the screen so that the gasket formed an air-tight seal on the outer edges of the filter. Then the filter holder frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- The programmable timer will be set for a sampling month of 1 hour or 24 hours. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number.).
- After sampling, the filter was transferred from the filter holder of the HVS to a sealed plastic bag and sent to the laboratory for weighting. The elapsed time was also recoded.
- Before weighting, all filters were equilibrated in desiccators for 24 hour with the temperature of $25^{\circ}\text{C} \pm 3^{\circ}\text{C}$ and the relative humidity (RH) $<50\% \pm 5\%$.

Maintenance & Calibration (QA/QC)

- HVS and their accessories should be maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVS should be calibrated at bi-monthly intervals.

Wind Data Monitoring

Wind data (wind speed and wind direction) were directly extracted from Wetland Park Station of Hong Kong Observatory. All wind data during this reporting month are shown in **Appendix G**.

2.3. Monitoring Parameters, Frequency and Duration

- 2.3.1.** Table 2.2 summarizes the monitoring parameters, monitoring duration and frequencies of impact air quality monitoring.

Table 2.2 Monitoring Parameters, Duration and Frequencies of Impact Air Quality Monitoring

Parameter	Duration	Frequency
1-hr TSP	1 hr (0800-1900)	Three times per 6 days
24-hr TSP	24 hr	Once per 6 days

- 2.3.2.** In this reporting period, a total of 15 occasions of 1-hour TSP monitoring and 5 events of 24-hour TSP monitoring were undertaken and the schedule was shown in **Table 2.3**

Table 2.3 Time Schedule of Impact Air Quality Monitoring

January 2019						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2	3	4 ▼	5
6	7	8	9	10 ▼	11	12
13	14	15	16 ▼	17	18	19
20	21	22 ▼	23	24	25	26
27	28 ▼	29	30	31		

Remark: (▼) = Air quality monitoring carried out by ET

2.4. Action and Limit Levels

The criteria for Action and Limit levels have been set out in the contract document of the Project as follows:

Table 2.4 The criteria of Action and Limit Levels for Air Quality

Parameters	Action	Limit
1-hour TSP Level ($\mu\text{g}/\text{m}^3$)	For baseline level $\leq 384\mu\text{g}/\text{m}^3$, Action level = (baseline level plus*1.3 + Limit Level) / 2	500 $\mu\text{g}/\text{m}^3$
	For baseline level $>384\mu\text{g}/\text{m}^3$, Action level = Limit Level	
24-hour TSP Level ($\mu\text{g}/\text{m}^3$)	For baseline level $< 200\mu\text{g}/\text{m}^3$, Action level = (baseline level plus*1.3 + Limit Level) / 2	260 $\mu\text{g}/\text{m}^3$
	For baseline level $\geq 200\mu\text{g}/\text{m}^3$, Action level = Limit Level	

Following the criteria shown in **Table 2.4**, the Action and Limit levels for 1-hour TSP derived as illustrated in **Table 2.5**.

Table 2.5 Action and Limit Levels for 1-hour TSP and 24-hour TSP

Air Quality Monitoring Station	1-hr TSP ($\mu\text{g}/\text{m}^3$)		24-hr TSP ($\mu\text{g}/\text{m}^3$)	
	Action Level	Limit Level	Action Level	Limit Level
ASR1a	309	500	260	260
ASR2b	292	500	228	260

2.5. Results and Observations

2.5.1. 1-hour and 24-hour TSP Monitoring Results

Monitoring data of both 1-hour and 24-hour TSP monitoring carried out in this reporting month are summarized in **Appendix D2**. Graphical presentation of 1-hour and 24-hour TSP monitoring results for the reporting month is shown in **Appendix D3**. Wind data included wind speed and wind direction was extracted from Wetland Park Station of Hong Kong Observatory during this reporting month and is presented in **Appendix G**.

No exceedance of Action and Limit Level of 1-hr TSP and 24-hour TSP monitoring results was recorded during the reporting month.

2.5.2. Observation

Generally, 1-hour TSP and 24-hour TSP monitoring results fluctuated well below the Action Level in this reporting period. The major dust source observed near the monitoring stations was mainly from vehicles passing by the container yards and general earth works. It can be concluded that the contractor implemented sufficient dust mitigation measures during this reporting month.

2.6. Event and Action Plan

If the impact monitoring results exceed the Action and Limit Levels, the actions specified in **Table 2.6** shall be carried out.

Table 2.6 Event and Action Plan for Air Quality (Dust) during Construction Phase

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded for one sample	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Action Level being exceeded for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency to daily; 5. Discuss with IEC and Contractor on remedial actions required; 6. If exceedance continues, arrange meeting with IEC and ER; 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial actions to IEC within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
Limit Level being exceeded for one sample	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC, ER and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with Contractor on the possible mitigation measures; 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Check monitoring data and Contractor's working methods; 4. Discuss with 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to ER within 3 working days of notification; 3. Implement the agreed

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
	effectiveness of Contractor's remedial actions; 8. Keep EPD and ER informed of the results.	6. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly.	IEC and Contractor on potential remedial actions; 4. Ensure remedial actions properly implemented.	proposals; 4. Amend proposal if appropriate.
Limit Level being exceeded for two or more consecutive samples	1. Identify source; 2. Inform IEC, ER and EPD the causes & actions taken for the exceedance s; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Investigate the causes of exceedance; 6. Arrange meeting with EPD and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with Contractor on the possible mitigation measures; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Supervise the implementation of mitigation measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 4. Discuss with IEC and the Contractor on potential remedial actions; 5. Review Contractor's remedial actions whenever necessary to assure their effectiveness; 6. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not resolved; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

3. NOISE MONITORING

3.1. Monitoring Requirements

- 3.1.1. Noise levels (L_{eq} , L_{10} and L_{90}) were monitored in the reporting month in accordance with the EM&A Manual.

3.2. Monitoring Equipment

Sound level meters used for impact noise monitoring were Type 1 sound level meters capable of giving a continuous readout of the noise level reading including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x). They complied with International Electro technical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 3.1** summarized the noise monitoring equipment model used during the baseline monitoring. Copies of calibration certificates for noise meters and calibrators were attached in **Appendix E1**.

Table 3.1 Noise Monitoring Equipment

Noise Monitoring Equipment	Model
Sound Level Meter	Rion NL-52
Sound Level Calibrator	Castle GA607

3.3. Monitoring Duration and Frequency

- 3.3.1. Impact noise monitoring for the A-weighted levels L_{eq} , L_{10} and L_{90} in 30-minute interval was recorded once per 6 days.
- 3.3.2. In this reporting period, a total of 5 occasions of noise monitoring were undertaken and the schedule was shown in **Table 3.2**

Table 3.2 Time Schedule of Impact Noise Monitoring

January 2019						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2	3	4 ▼	5
6	7	8	9	10 ▼	11	12
13	14	15	16 ▼	17	18	19
20	21	22 ▼	23	24	25	26
27	28 ▼	29	30	31		

Remark: (▼) = Noise monitoring carried out by ET

3.4. Monitoring Locations

Two noise monitoring stations, NSR1a (晉榮貨櫃服務有限公司) and NSR2b (永康貨櫃服務有限公司) which shown in **Figure 1**, were required to perform impact noise monitoring during this reporting period.

The impact noise monitoring programme was summarized in **Table 3.3**.

Table 3.3 Noise Monitoring Stations

Noise monitoring station	Type of Measurement
NSR1a	Façade
NSR2b	Façade

3.5. Monitoring Methodology

Instrumentation

Integrating Sound Level Meters were employed for noise monitoring.

Operation/Analysis Procedures

- The Sound Level Meter was set on a tripod at a height of 1.2m above the ground.
- For free field measurement, the meter was positioned away from any nearby reflective surfaces.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - Frequency weighting : A
 - Time weighting : Fast
 - Time measurement : 30 mins
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1000HZ. If the difference in the calibration level before and after measurement was more than 1 dB(A), the measurement would be considered invalid and repeat measurement would be required after re-calibration or repair of the equipment.
- During the monitoring period, the L_{eq} , L_{10} and L_{90} were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- 3dB(A) correction had been added to the results if noise measurements were free-field.
- Noise monitoring would be cancelled in the presence of fog, rain, storm, wind with a steady speed exceeding 5m/s, or wind gusts exceeding 10m/s.

Maintenance and Calibration (QA/QC)

- The microphone head of the sound level meter and calibrator are cleaned with soft cloth at quarterly intervals.
- The meters are sent to the HOKLAS accredited laboratory or equivalent to check and calibrated at yearly intervals.

3.6. Actions and Limit Level

The Action and Limit Levels were established in **Table 3.4** for noise monitoring.

Table 3.4 Action and Limit Levels for Noise Monitoring

Time Period	Action	Limit
0700 –1900 hrs normal weekdays	When one documented complaint is received	75 dB(A)*

Remark: (*)70dB(A) for schools and 65dB(A) for schools during school examination period

3.7. Results and Observations

3.7.1. Results

Monitoring data of noise monitoring carried out in this reporting month are summarized in **Appendix E2**. Graphical presentation of noise monitoring results for the reporting month is shown in **Appendix E3**.

No exceedance of Action and Limit Level of noise monitoring results was recorded during the reporting month.

3.7.2. Observation

The noise monitoring data were found to be lower than the limit level. The major noise source during the monitoring event was the vehicles passing through the container yard entrance and the general earth works inside the construction site.

3.8. Event and Action Plan

If the impact monitoring results exceed the Action and Limit Levels, the actions specified in **Table 3.5** shall be carried out.

Table 3.5 Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level	<ol style="list-style-type: none"> 1. Notify IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC and Contractor; 4. Discuss with the Contractor and formulate remedial measures ; 5. Increase monitoring frequency to check the effectiveness of mitigation measures. 	<ol style="list-style-type: none"> 1. Review the analyzed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure mitigation measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposal to IEC; 2. Implement noise mitigation proposals.
Limit level	<ol style="list-style-type: none"> 1. Notify IEC, ER, EPD & Contractor; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure mitigation measures are properly implemented; 5. If exceedances continues, consider what 	<ol style="list-style-type: none"> 1. Undertake immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant

	<p>ER and EPD the causes and actions taken for the exceedances;</p> <p>7. Assess the effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</p> <p>8. If exceedance stops, cease additional monitoring.</p>		<p>portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</p>	<p>portion of works as determined by ER, until the exceedance is abated.</p>
--	---	--	--	--

4. WATER QUALITY MONITORING

4.1. Monitoring Requirements

- 4.1.1. Water quality was monitored in the reporting month in accordance with the EM&A Manual at one alternative water quality monitoring station, R1b (at Tin Shui Wai Nullah) which shown in **Figure 2**.

4.2. Monitoring Methodology and Equipment

For In-situ Water Quality Measurement

Dissolved Oxygen (DO) measuring equipment

A portable, weatherproof DO-measuring meter with built-in salinity compensation (e.g. YSI 85, YSI Pro 2030 or equivalent) was used in the baseline monitoring. It can be capable for measuring dissolved oxygen level in the range of 0-20 mg/L and 0-200 % saturation.

For Water Sampling and Sample Analysis

Water Sampler

A water sampler comprising a metal bucket was lowered into the water body.

Water Container

The sample container, made by high-density polythene, was rinsed with a portion of the water sample. The water sample was then transferred to the container, labelled with a unique sample ID and sealed with a screw cap. The water samples were stored in a cool box maintained at 4°C. The water samples will then be delivered to Environmental Laboratory of ETS-Testconsult Ltd (HOKLAS Registration No. 022) on the same day for analysis according to the Standard Method APHA 19ed.

The summary of testing methods of testing parameters required was shown in **Table 4.1**.

Table 4.1 Summary of Testing Procedures for water samples

Parameters	Testing Procedure	Detection Limit
Turbidity	Dissolved Oxygen Meter Measurement	0.1 NTU
Dissolved Oxygen	In house method refer to APHA 19 th ed 2130 B	0.01 mg/L
Total suspended solids	In house method refer to APHA 19 th ed 2540D	0.1 mg/L

4.3. Monitoring Frequency

- 4.3.1. Water samples were collected 3 times per week in 1 monitoring station. Three parameters including turbidity, dissolved oxygen and total suspended solids would be tested.

Table 4.2 Monitoring Frequency of Water Quality Monitoring

Parameters	Frequency	No. of sampling stations
Turbidity	3 times per week	1 station
Dissolved Oxygen		
Total suspended solids		

- 4.3.2. In this reporting period, a total of 13 occasions of water quality monitoring were undertaken and the schedule was shown in **Table 4.3**

Table 4.3 Time Schedule of Impact Water Quality Monitoring

January 2019						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
		1	2	3 ▼	4	5 ▼
6	7	8 ▼	9	10 ▼	11	12 ▼
13	14	15 ▼	16	17 ▼	18	19 ▼
20	21	22 ▼	23	24 ▼	25	26 ▼
27	28	29 ▼	30	31 ▼		

Remark: (▼) = Water quality monitoring carried out by ET.

4.4. Quality Assurance (QA) / Quality Control (QC)

For in-situ measurements, at each measurement / sampling, two consecutive measurements of turbidity and dissolved oxygen (DO) were taken. The probes were retrieved out of the water after the first measurement and then re-deployed for the second measurement. If the difference between the first and second measurement is greater than 25% the reading will be discarded and the measurements will be repeated.

For laboratory analysis of water, test method of all test parameters and the QA/QC samples were carried out in accordance with the requirements of HOKLAS.

For our QA/QC procedure, one QC sample, one duplicate sample and one sample spike of every batch of 20 samples were analyzed.

The calibration certifications of water quality monitoring equipments were shown in **Appendix F1**.

4.5. Actions and Limit Levels

The criteria for Action and Limit Levels have been set out as follows:

Table 4.4 The criteria of Action and Limit Levels for Water Quality

Parameters	Unit	Action Level	Limit Level
Turbidity	NTU	95%ile of baseline data	99%ile of baseline data
Dissolved Oxygen	mg/L	5%ile of baseline data	1%ile of baseline data
Suspended solids	mg/L	95%ile of baseline data	99%ile of baseline data

Following the criteria shown in **Table 4.4**, the Action and Limit Levels for monitoring parameters derived as illustrated in **Table 4.5**.

Table 4.5 Action and Limit Levels for Water Quality

Parameters	Unit	Action	Limit
Turbidity	NTU	19.8	20.5
Dissolved Oxygen	mg/L	1.84	1.81
Suspended Solid	mg/L	17.0	17.8

4.6. Result and Observation

4.6.1. Result

Monitoring data of water quality monitoring carried out in this reporting month are summarized in **Appendix F2**. Graphical presentation of the monitoring results for the reporting month is shown in **Appendix F3**.

No exceedance of Action and Limit Level of water quality monitoring results was recorded during the reporting month.

4.6.2. Observation

Generally, the turbidity and suspended solids were found to be lower than the action level. Besides, all results of dissolved oxygen measured in this reporting month were higher than the action level.

4.7. Event and Action Plan

If the impact monitoring results of the individual parameters exceed the Action and Limit Levels, the actions specified in **Table 4.6** shall be carried out.

Table 4.6 Event and Action Plan for Water Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC and 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IEC on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment 4. Consider changes of working methods; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER; 6. Implement the agreed mitigation



Event	Action			
	ET Leader	IEC	ER	Contractor
	6. Contractor; Repeat measurement on next day of exceedance.			measures.
Action Level being exceeded by more than two consecutive sampling days	1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC and Contractor; 6. Ensure mitigation measures are implemented; 7. Prepare to increase the monitoring frequency to daily; 8. Repeat measurement on next day of exceedance.	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC on the proposed mitigation measures; 2. Make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures.	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures.
Limit Level being exceeded by one sampling day	1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact;	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all



Event	Action			
	ET Leader	IEC	ER	Contractor
	3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level.	Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures.	working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures.	plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures.
Limit Level being exceeded by more than two consecutive sampling days	1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures; 5. Consider and instruct, if necessary, the	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation

Event	Action			
	ET Leader	IEC	ER	Contractor
	mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days.		Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit Level.	measures; 7. As directed by the ER, to slow down or to stop all or part of the marine work or construction activities.

5. ENVIRONMENTAL SITE INSPECTION AND AUDIT

5.1. Site Inspection

- 5.1.1. Site Inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control mitigation measures for the project. During the reporting period, site inspections were carried out on 04, 11, 18, 25 & 30 January 2019.
- 5.1.2. Observations for the site inspections within this reporting period are summarized in **Table 5.1** and inspection checklists are attached in **Appendix H**.

Table 5.1 Summary of observation of site inspections

Date	Observations/ Reminders	Follow-up Action	Closed Date
27 December 2018	1. Chemical containers without drip tray were observed.	1. Chemical containers were removed.	04 January 2019
04 January 2019	1. Stagnant water was observed at Portion P1.	1. Stagnant water was cleared at Portion P1.	11 January 2019
11 January 2019	--	--	--
18 January 2019	1. Chemical waste area was found without chemical label.	1. Correct chemical label was provided.	25 January 2019
25 January 2019	1. Water quality of Wetsep Tank should be improved.	2. Accumulated mud was cleaned.	30 January 2019
30 January 2019	--	--	--

5.2. Landscape and Visual Audit

- 5.2.1. Landscape and visual audits were undertaken at least once every two weeks throughout the construction period by a competent landscape architect. During the reporting period, audits were carried out on 11 and 25 January 2019.
- 5.2.2. Observations and reminders were summarized in the landscape and visual impact assessment checklists which are attached in **Appendix I**.

5.3. Advice on the Solid and Liquid Waste Management Status

5.3.1. All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) Material;
- Chemical Waste;
- General Refuse; and
- Excavated Soil

5.3.2. The quantities of waste for disposal in this Reporting Period are summarized in **Table 5.2** and **Table 5.3** and the Monthly Summary Waste Flow Table is shown in **Appendix J**. Whenever possible, materials were reused on-site as far as practicable.

Table 5.2 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
Reused in this Contract (Inert) (m ³)	0	--
Reused in other Projects (Inert) (m ³)	0	--
Disposed as Public Fill (Inert) (m ³)	988	Tuen Mun 38 Fill Bank

Table 5.3 Summary of Quantities of C&D Materials

Type of Waste	Quantity	Disposal Location
Recycled Metal (kg)	0	--
Recycled Paper / Cardboard Packing (kg)	0	--
Recycled Plastic (kg)	0	--
Chemical Wastes (kg)	0	--
General Refuses (m ³)	55,820	North East New Territories (NENT) Landfill

5.3.3. To control over the site performance on waste management, the Contractor shall ensure that all solid and liquid waste management works are in full compliance with the relevant license/permit requirements, such as the effluent discharge license and the chemical waste producer registration. The Contractor is also reminded to implement the recommended environmental mitigation measures according to the EM&A Manual based on actual site conditions.

5.4. Discharge License and Results of Effluent Monitoring

5.4.1. Effluent quality was monitored in the reporting month in accordance with the EM&A Manual at the discharge point. A discharge license under Water Pollution Control Ordinance was obtained by the Contractor upon commencement of the Project. Self-monitoring would be performed as per the requirement under the discharge license. According to the EM&A Manual, pH, chemical oxygen demand and total suspended solid are required to be analysed at least once every two week.

5.4.2. Effluent water samples were scheduled to be collected on 03 and 15 January 2019. As there was no water discharged from 29 to 31 January 2019 and only Wetsep at P1b was operated on 03 January 2019, the effluent water sample was sampled at P1b only on 03 January 2019. The required testing parameter including pH, chemical oxygen demand and total suspended solid were carried out in a HOKLAS laboratory. The methods of chemical oxygen demand and total suspended solid determination follow APHA 19ed 5220 B and APHA 19ed 2540 D respectively. The laboratory reports for the discharge water are presented in **Appendix N**.

5.4.3. For effluent quality monitoring as per the discharge license requirement, the results complied with the discharge license requirement.

5.5. Environmental Licenses and Permits

- 5.5.1. The valid environmental licenses and permits during the reporting period are summarized in **Appendix K**.

5.6. Implementation Status of Environmental Mitigation Measures

- 5.6.1. The environmental mitigation measures that recommended in the Environmental Monitoring and Audit Manual covered the issues of dust, noise, water and waste and they are summarized as following:

Dust Mitigation Measures

- a. The working area for the uprooting of trees, shrubs, or vegetation or for the removal of boulders, poles, pillars or temporary or permanent structures should be sprayed with water or a dust suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;
- b. All demolished items (including trees, shrubs, vegetation, boulders, poles, pillars, structures, debris, rubbish and other items arising from site clearance) that may dislodge dust particles should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition;
- c. Vehicle washing facilities including a high pressure water jet should be provided at every discernible or designated vehicle exit point;
- d. The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;
- e. Where a site boundary adjoins a road, street, service and or other area accessible to the public, hoarding of not less than 2.4m from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit;
- f. Every main haul road (i.e. any course inside a construction site having a vehicle passing rate of higher than 4 in any 30 minutes) should be paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical so as to maintain the entire road surface wet;
- g. The portion of any road leading only to a construction site that is within 30m of a discernible or designated vehicle entrance or exit should be kept clear of dusty materials;
- h. Immediately before leaving a construction site, every vehicle should be washed to remove any dusty materials from its body and wheels;
- i. Where a vehicle leaving a construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle;
- j. The working area of any excavation or earth moving operation should be sprayed with water or a dusty suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;
- k. Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within 6 months after the last construction activity on the construction site or part of the construction site where the exposed earth lies;
- l. Any stockpile of dusty material should be either covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or a dust suppression chemical so as to maintain the entire surface wet.

Noise Mitigation Measures

- a. Quiet plants should be used in order to reduce the noise impacts to protect the nearby NSRs.
- b. Temporary and Movable Noise Barriers should be used in order to reduce the noise impact to the surrounding sensitive receivers
- c. The contractor should site noisy equipment and activities as far from sensitive receivers as practical.
- d. Idle equipment should be turned off or throttled down.
- e. Construction activities should be planned so that parallel operation of several sets of equipment close to a given receiver is avoided
- f. Construction plant should be properly maintained and operated.

Water Quality Mitigation Measures

- a. Exposed stockpiles should be covered with tarpaulin or impervious sheets before a rainstorm occurs;
- b. The exposed soil surfaces should also be properly protected to minimize dust emission;
- c. The stockpiles of materials should be placed in the locations away from the drainage channel so as to avoid releasing materials into the channel;
- d. Wheel washing facilities should be provided at site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles;
- e. Provision of site drainage systems and treatment facilities would be required to minimize the water pollution;
- f. A discharge license needs to be applied from EPD for discharging effluent from the construction site;
- g. The treated effluent quality is required to meet the requirements specified in the discharge license;
- h. Provision of chemical toilets is required to collect sewage from workforce. The chemical toilets should be cleaned on a regular basis;
- i. A licensed waste collector should be employed to clean the chemical toilets and temporary storage tank on a regular basis;
- j. Illegal disposal of chemicals should be strictly prohibited;
- k. Registration as a chemical waste producer is required if chemical wastes are generated and need to be disposed of. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes;
- l. Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance should be used as a guideline for handling chemical wastes;
- m. The impact from accidental spillage of chemicals can be effectively controlled through good management practices.

Waste Management Mitigation Measures

- a. Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;
- b. To encourage collection of aluminium cans by individual collectors, separate bins should be provided to segregate this waste from other general refuse generated by the workforce;
- c. Any unused chemicals or those with remaining functional capacity should be recycled;
- d. Prior to disposal of C&D waste, it is recommended that wood, steel and other metals be separated for re-use and/or recycling and inert waste as fill material to minimize the quantity of waste to be disposed of to landfill;
- e. Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and
- f. Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.

5.6.2. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in **Appendix L**. Most of the necessary mitigation measures were implemented properly. Any deficiencies were noted in the remarks of the schedule.

5.7. Summary of Exceedance of the Environmental Quality Performance Limit

5.7.1. There was no Action and Limit level exceedance of 1-hour and 24-hr TSP monitoring was recorded at station ASR1a and ASR2b during this reporting month.

5.7.2. There was no Action and Limit Level exceedance for noise recorded at station NSR1a and NSR2b during the reporting period.

5.7.3. There was no Action and Limit Level exceedance for water quality monitoring recorded at station R1b during the reporting period.

5.8. Summary of Complaints, Notification of Summons and Successful Prosecution

5.8.1. There were no complaints received during the reporting period.

5.8.2. There were no notifications of summons or prosecutions received during the reporting period.

5.8.3. A summary of environmental complaints, notifications of summons and successful prosecutions was given in **Table 5.4**.

Table 5.4 Summary of Environmental Complaints Notification of Summons and Successful Prosecution

Reporting Period	Cumulative Statistic		
	Complaints	Notifications of summons	Successful prosecutions
The reporting period	0	0	0
From commencement date of construction to end of reporting month	0	0	0

6. FUTURE KEY ISSUES

6.1. Construction Programme for the Coming Months

6.1.1. As informed by the Contractor, the major construction activities for February 2019 are included:

- Substructure (rc structure);
- Backfilling;
- Superstructure (rc and metalworks);
- Water Tightness Test;
- Internal ABWF – CEPT;
- Substructure (ELS & Bulk excavation);
- Removal of ELS;
- Water Tightness Test;
- ABWF – UV Disinfection Facility, Sludge Dewatering Building, Administration Building & Maintenance Workshop, EB4 Transformer Room, Electrical Building No.4;
- Pile Loading Test;
- Post-Drilling;
- Bar Screen Installation;
- Site Formation along Boundary Wall (Perimeter);
- Slope works and Retaining Wall (Eastern Portion);
- Slope works and Retaining Wall (Northern Portion);
- Drainage Inlet connection (Diversion of Three Existing Sewage Rising Mains);
- Drainage Outlet connection to the Existing Stormwater Drainage System along Ha Tsuen Road;
- CLP Cable Duct and Draw Pits (within the Site);
- EVA (Road & Drainage);
- RC Trench and Odour Pipe (DO1, DO2);
- Process Pipe;
- Drainage Pipe (Stormwater) incl. Surface Drainage at Site Platform & On Slope;
- Emergency By-Pass Pipe;
- Sewage Pipe;
- Cable Duct and Draw Pits;
- WSD External Watermain Laying Works;
- Internal Watermain Laying Works



6.2. Key Issues for the Coming Month

Key issues to be considered in the coming month include:

- Chemical and waste management;
- Treatment of runoff and wastewater prior to discharge; and
- Dust and Noise generated from construction activities;

Mitigation measures to be required in the coming month:

Air Quality Impact

- To provide adequate water spraying in the worksite;
- To operate and maintain automatic wheel washing facilities properly;
- To provide road sweeping site entrance and public roads outside site entrance;
- To ensure implementation of the dust mitigation measures for the site activities;
- To maintain proper operation of the mist spraying system;
- To provide proper maintenance for vehicles and machines on site; and
- To investigate any other dust sources around the air sensitive receivers

Noise

- To switch off equipment if not in use;
- To operate silent equipment;
- To identify the noise sources inside and outside of the site; and
- To follow up any exceedance caused by the construction work inside the worksite

Water Quality Impact

- To ensure the drainage system was maintained properly;
- To maintain the existing silt trap to ensure good efficiency of wheel wash facilities;
- To avoid stagnant water in the drip trays due to rainfall;
- To avoid any stagnant water or provide insecticide to avoid mosquito breeding

Chemical and Waste Management

- To remove waste from the site regularly;
- To properly store and handle chemical wastes on site;
- To implement trip ticket system for all the imported public fill and general refuse disposal;
- To maintain proper housekeeping;
- To identify C&D material by packaging, labelling, storage, transportation and disposal in accordance with statutory regulations.

6.3. Environmental Monitoring and Site Inspection Schedule for the Coming Month

- 6.3.1. The tentative schedule for environmental monitoring and site inspection schedule for February 2019 is provided in **Appendix M**.

7. CONCLUSION


7.1. Conclusions

- 7.1.1. There was no Action and Limit level exceedance of 1-hour and 24-hr TSP monitoring was recorded at station ASR1a and ASR2b during this reporting month.
- 7.1.2. There was no Action and Limit Level exceedance for noise recorded at station NSR1a and NSR2b during the reporting period.
- 7.1.3. There was no Action and Limit Level exceedance for water quality monitoring recorded at station R1b during the reporting period.
- 7.1.4. There were no complaints received during the reporting period.
- 7.1.5. There were no notifications of summons or prosecutions received during the reporting period.

- END OF REPORT -


Appendix A

Location of Works Areas

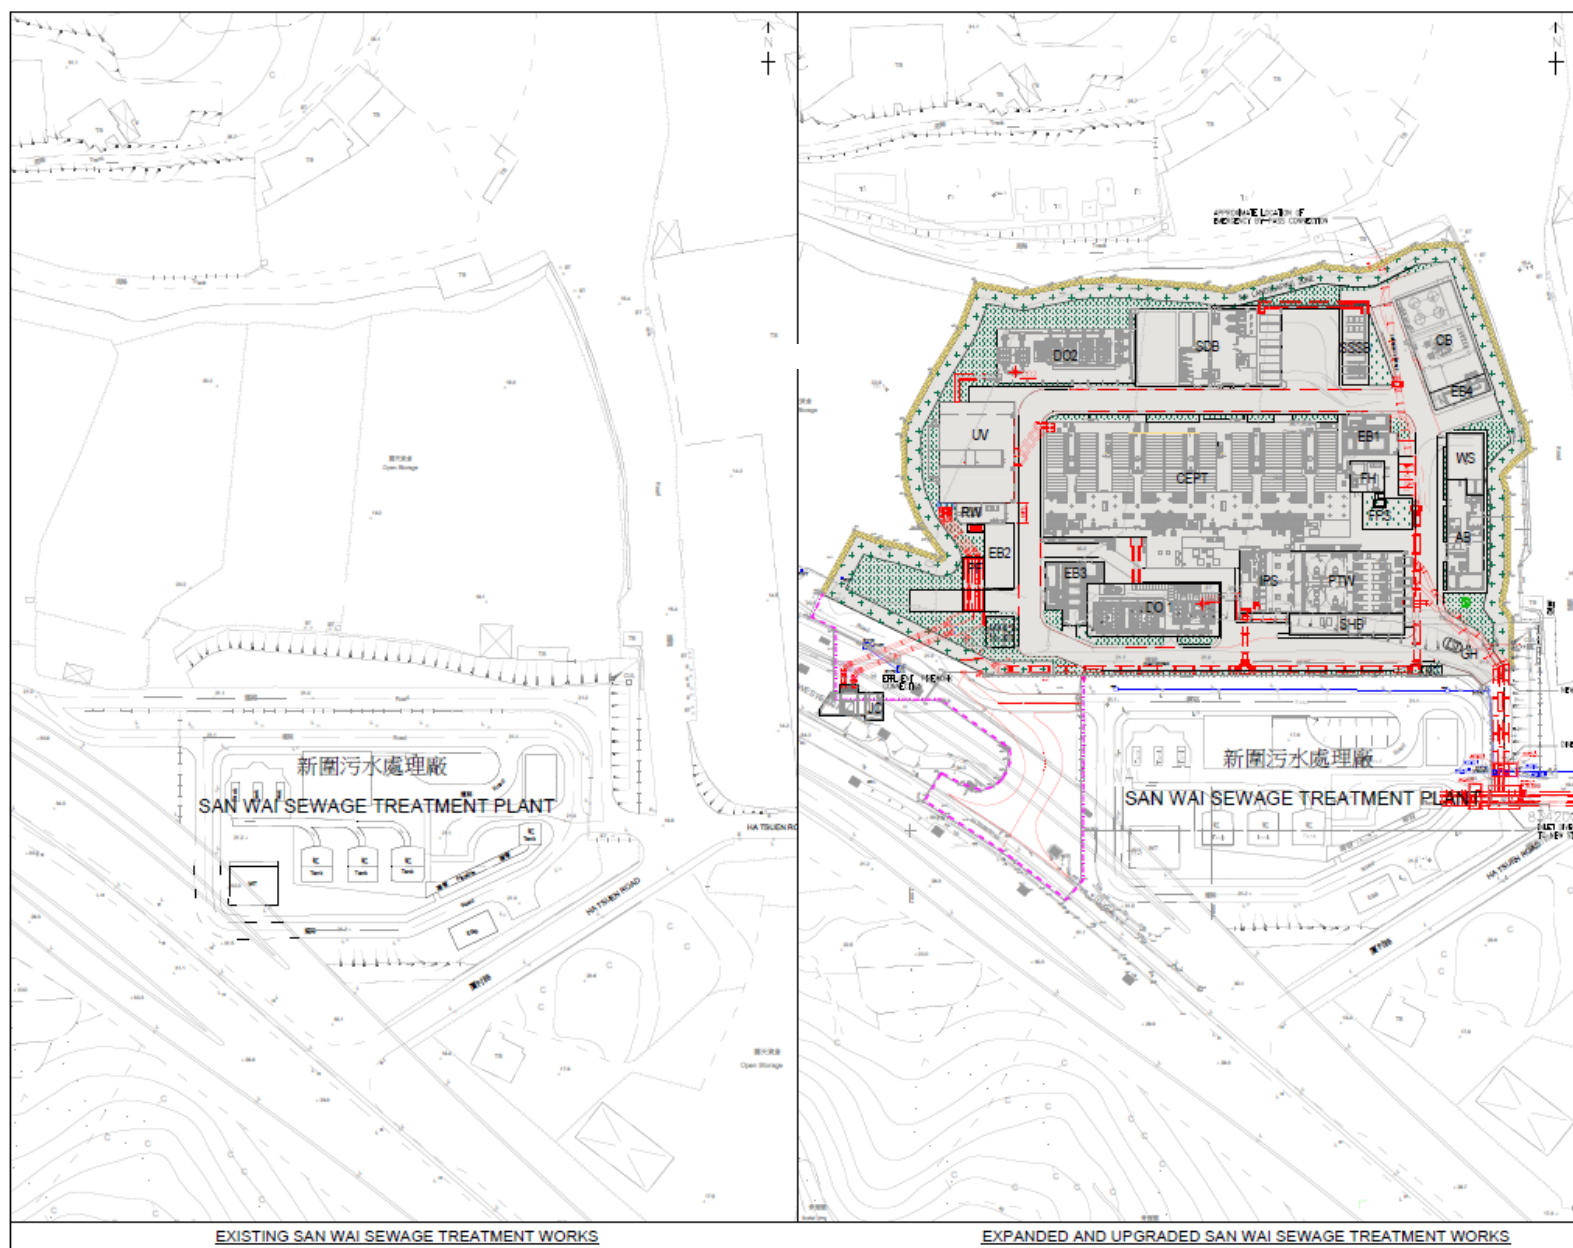

Appendix B

Project Organization Chart

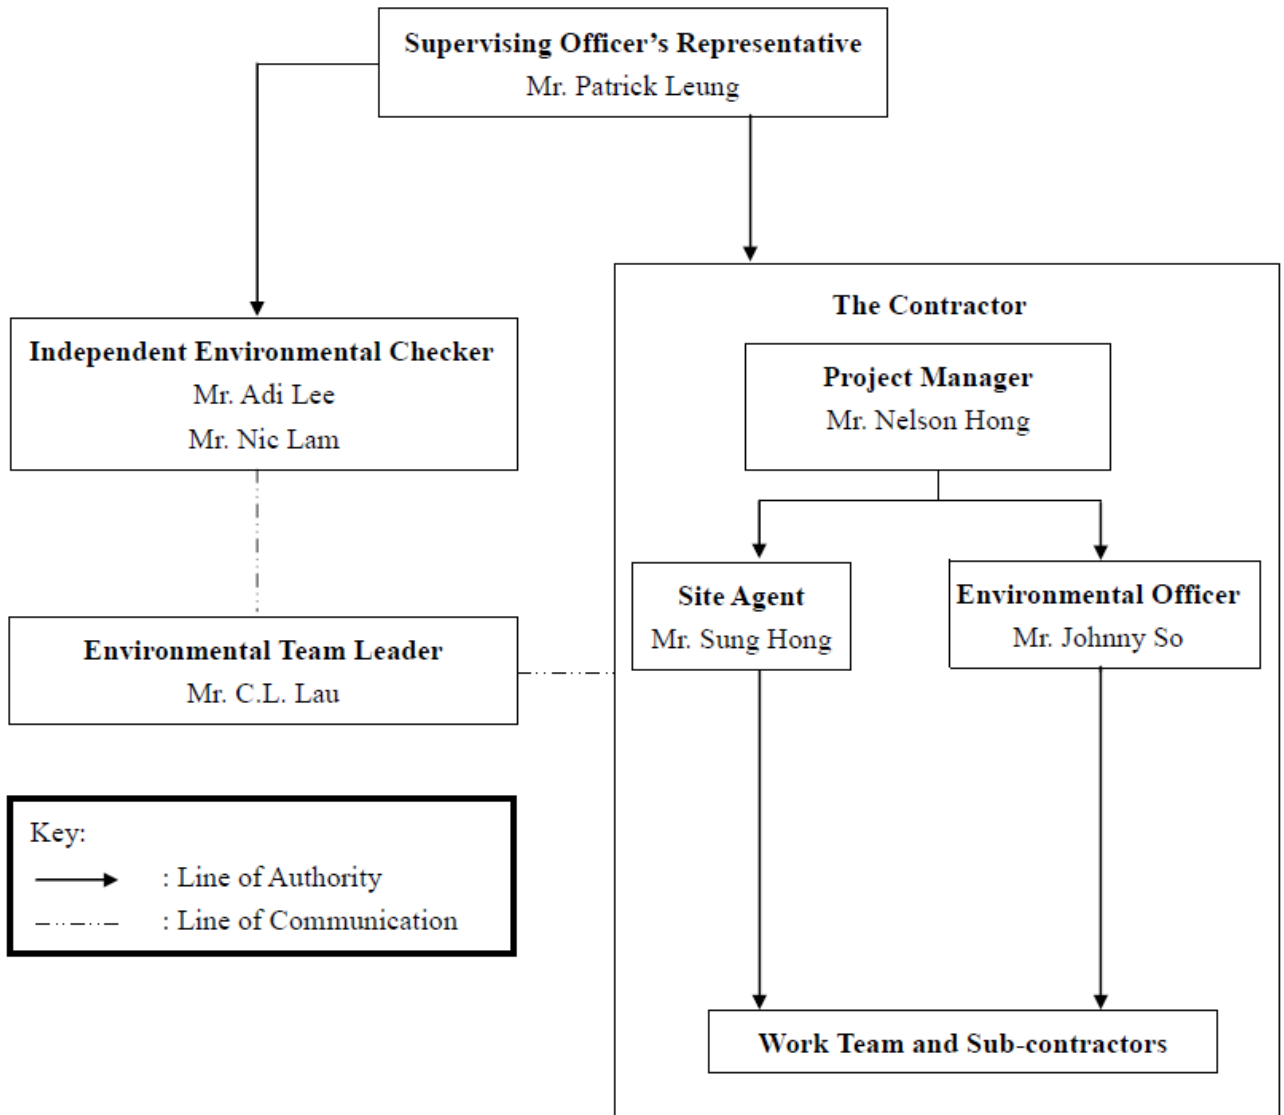

Appendix C

Construction Programme

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (31-Jan-19)			PAGE 1 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Jan	Feb	Mar	Apr	May
San Wai Sewage Treatment Works Phase 1 - Rev 10 MP (Update as of 31 Jan 2019) matc		1672	27-May-16 A	23-Dec-20					
Key Date		1672	27-May-16 A	23-Dec-20					
Commencement & Completion of Works		1672	27-May-16 A	23-Dec-20					
KD150	Section 1 - Handover to Home Affairs Department for Maintenance	1120	30-Nov-17 A	23-Dec-20					
KD160	Section 2 - Period of Works (FOT P.3 of 67, 71) - Including 88.5 Days Granted EOT	1672	27-May-16 A	23-Dec-20					
Plant Room Handover Dates To E&M Installation		69	18-Feb-19	28-Apr-19					
KD300	Administration Building & Maintenance Workshop (AB & WS)	0	28-Feb-19				◆ Administration Building & Maintenance Workshop (AB & WS)		
KD304	Solid Handling Building (SHB)	0	20-Apr-19				◆ Solid Handling Building (SHB)		
KD308	Chemically Enhanced Primary Treatment (CEPT)	0	18-Feb-19			◆ Chemically Enhanced Primary Treatment (CEPT)			
KD310	Deodorization Facilities No.1 (DO 1)	0	23-Apr-19				◆ Deodorization Facilities No.1 (DO 1)		
KD314	Sludge Dewatering Building (SDB)	0	25-Mar-19				◆ Sludge Dewatering Building (SDB)		
KD316	UV Disinfection Facilities (UV)	0	04-Apr-19				◆ UV Disinfection Facilities (UV)		
KD320	Payment Flowmeter Chamber (PF)	0	18-Apr-19				◆ Payment Flowmeter Chamber (PF)		
KD324	Chemical Building (CB)	0	27-Apr-19				◆ Chemical Building (CB)		
KD326	Electrical Building No.1 (EB1)	0	23-Apr-19				◆ Electrical Building No.1 (EB1)		
KD328	Electrical Building No.2 (EB2)	0	09-Apr-19				◆ Electrical Building No.2 (EB2)		
KD330	Electrical Building No.3 (EB3)	0	05-Apr-19				◆ Electrical Building No.3 (EB3)		
KD331	Electrical Building No.4 (EB4)	0	08-Mar-19			◆ Electrical Building No.4 (EB4)			
KD332	DG Store and Chemical Waste Storage Building (DG) and Irrigation & Cleansing Water Pump Room (ICW)	0	28-Apr-19				◆ DG Store and Chemical Waste Storage Building (DG) and Irrigation & Cleansing Water Pump Room (ICW)		
Preliminaries & General Requirement		1362	01-Apr-17 A	23-Dec-20					
Contractor Requirement		1362	01-Apr-17 A	23-Dec-20					
PS465	Impact Monitoring	1275	27-Jun-17 A	22-Dec-20					
PS485	Site Drainage Plan Implementation	1362	01-Apr-17 A	23-Dec-20					
Design & Design Checking of Permanent Works		1587	26-Jun-16 A	29-Oct-20					
Statutory Submission		1325	15-Mar-17 A	29-Oct-20					
DS150	Application of Discharge License for Operation	180	08-Feb-19	06-Aug-19					
DS166	CLP - Photovoltaic Panel Connection	407	24-Dec-17 A	03-Feb-19					
DS173	PCCW - Telephone Lines and Megalink	614	27-Jun-17 A	03-Mar-19					
DS174	PCCW - Telephone Lines for CLP Summation Metering	556	28-Jul-17 A	03-Feb-19					
DS177	EMSD - Passenger Lift	326	29-May-18 A	20-Apr-19					
DS180	EPO - Application for Emergency Generator Flue Gas Discharge License	180	28-Nov-18 A	26-May-19					
DS195	BEAM Plus - Final Assessment (FA)	974	01-Mar-18 A	29-Oct-20					
DS200	ArchSD - V-CAB and DAP Submission and Approval	695	15-Mar-17 A	07-Feb-19					
AIP / DDA Submission & Approval		1032	26-Jun-16 A	23-Apr-19					
DS410	Review & Revisions of Design Plan	960	26-Jun-16 A	10-Feb-19					
Design Memorandum (AIP1 / DDA1)		344	13-May-18 A	22-Apr-19					
DS505	DDA1 - Design Memorandum - Design Preparation to SO Approval	344	13-May-18 A	22-Apr-19					
Global Design		832	06-Jan-17 A	17-Apr-19					
Electrical Power Supply System (AIP20 / DDA20ABCDE)		714	24-Apr-17 A	08-Apr-19					
DG1891	DDA20A - Electrical Power Supply System - Design Preparation to SO Approval	689	24-Apr-17 A	14-Mar-19					

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

ATAL

Swire

HEC

ATAL-Degremont-China Harbour Joint Venture

TASK filter: 3 Months Rolling Programme.

CONTRACT NO. DC/2013/10 DESIGN, BUILD & OPERATE

SAN WAI SEWAGE TREATMENT WORKS - PHASE 1

MASTER PROGRAMME Rev 10 (31 January 2019)

THREE (3) MONTHS ROLLING PROGRAMME

Date	Revision	Checked	Approved
31-Jan-19	Three (3) Months Rolling Programme...		

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 31-Jan-19)			PAGE 2 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	Jan	Feb	2019 Mar	Apr	May
DG3880	DDA20B - UPS System - Design Preparation to SO Approval	686	24-Apr-17 A	10-Mar-19					
DG3896	DDA20C - Earthing and Lightning System - Design Preparation to SO Approval	686	24-Apr-17 A	11-Mar-19					
DG3912	DDA20D - Energy Efficiency - Design Preparation to SO Approval	714	24-Apr-17 A	08-Apr-19					
Control and Monitoring System (AIP21 / DDA21ABCDE)		822	12-Jan-17 A	13-Apr-19					
DG1924	DDA21A - Process & Instrumentation Diagram (P&ID) - Design Preparation to SO Approval	791	12-Jan-17 A	13-Mar-19					
DG1940	DDA21B - System Control Philosophy - Design Preparation to SO Approval	728	20-Mar-17 A	17-Mar-19					
DG1966	DDA21C - Functional Design Specification - Design Preparation to SO Approval	696	03-Apr-17 A	28-Feb-19					
DG1972	DDA21D - PLC, SCADA & I/O Allocation Schedules - Design Preparation to SO Approval	676	23-Apr-17 A	28-Feb-19					
DG1988	DDA21E - SCADA Graphic Interface - Design Preparation to SO Approval	652	01-Jul-17 A	13-Apr-19					
Landscaping Works (AIP22 / DDA22AB)		800	06-Jan-17 A	16-Mar-19					
DG1260	DDA22A - Landscaping Works (Green Roof) - Design Preparation to SO Approval	761	06-Jan-17 A	05-Feb-19					
DG1274	DDA22B - Landscaping Works (Site Wide) - Design Preparation to SO Approval	622	03-Jul-17 A	16-Mar-19					
Testing and Commissioning Plan (AIP23 / DDA23)		333	22-Apr-18 A	20-Mar-19					
DG3305	DDA23 - Detailed Testing & Commissioning Plan - Design Preparation to SO Approval	333	22-Apr-18 A	20-Mar-19					
General Notes Drawings for Foundation and Civil & Structural (AIP24AB / DDA24AB)		737	22-Feb-17 A	28-Feb-19					
General Notes Drawings for Civil & Structural (AIP24B / DDA24BC)		737	22-Feb-17 A	28-Feb-19					
DG3706	DDA24C - Typical Details for Architecture - Design Preparation to SO Approval	737	22-Feb-17 A	28-Feb-19					
Site Formation (AIP26 / DDA26)		775	14-Jan-17 A	28-Feb-19					
DG660	DDA26 - Site Formation - Design Preparation to SO Approval	775	14-Jan-17 A	28-Feb-19					
Road Works (AIP27A / DDA27A)		707	23-Mar-17 A	27-Feb-19					
DG1060	DDA27A - Road Works - Design Preparation to SO Approval	707	23-Mar-17 A	27-Feb-19					
Sewerage and Drainage Works (AIP27B / DDA27BC1C2DEF)		746	21-Feb-17 A	08-Mar-19					
Civil and Structural Design (AIP27B / DDA27BCD)		746	21-Feb-17 A	08-Mar-19					
DG990	DDA27B - Sewerage and Drainage Works - Design Preparation to SO Approval	737	21-Feb-17 A	27-Feb-19					
DG998	DDA27D - Detailed Design Report for Pipe Trenches - C&S - Design Preparation to SO Approval	670	08-May-17 A	08-Mar-19					
Boundary Wall & Entrance (AIP28 / DDA28AB)		804	03-Feb-17 A	17-Apr-19					
DG1160	DDA28A - Slopes and Retaining Wall - Design Preparation to SO Approval	730	03-Feb-17 A	02-Feb-19					
DG1195	DDA28B - Boundary Wall & Entrance - Design Preparation to SO Approval	670	17-Jun-17 A	17-Apr-19					
Site Wide Utility (AIP30 / DDA30ABCEFGI)		788	30-Jan-17 A	29-Mar-19					
DG3515	DDA30A - Site Wide Security Access Control & Communication System - Design Preparation to SO Approval	774	30-Jan-17 A	14-Mar-19					
DG3774	DDA30B - Site Wide Utility (U/G Pipework, Ductwork, Cable Route, Cable Draw Pit) - Design Preparation to SO Approval	605	08-Jun-17 A	02-Feb-19					
DG3788	DDA30C - Fire Services System and Street Fire Hydrant System - Design Preparation to SO Approval	616	08-Jun-17 A	13-Feb-19					
DG3816	DDA30E - Site Wide Utility (Road Lighting) - Design Preparation to SO Approval	630	23-Jun-17 A	14-Mar-19					
DG3830	DDA30F - Typical Electrical Installation Drawings - Design Preparation to SO Approval	659	08-Jun-17 A	28-Mar-19					
DG3844	DDA30G - Typical Building Services Installation Drawings - Design Preparation to SO Approval	644	23-Jun-17 A	29-Mar-19					
HAZOP Report (DDA31B)		520	01-Sep-17 A	02-Feb-19					
DG3545	DDA31B - Hazardous Zoning Classification Report - Design Preparation to SO Approval	520	01-Sep-17 A	02-Feb-19					
ELS / Bulk Excavation (Temporary Works)		514	04-Sep-17 A	31-Jan-19					
ELS for Inlet Pipe Connection		514	04-Sep-17 A	31-Jan-19					
DG3755	ELS for Inlet Pipe Connection - Design Preparation to DC and SO Approval	514	04-Sep-17 A	31-Jan-19					
Miscellaneous Design		592	03-Jul-17 A	14-Feb-19					
Equipment Schedules (DDA32A)		579	03-Jul-17 A	01-Feb-19					
DG2012	DDA32A - Equipment Schedules - Design Preparation to SO Approval	579	03-Jul-17 A	01-Feb-19					
Penstock & Stoplogs Schedules (DDA32B)		584	03-Jul-17 A	06-Feb-19					
DG3216	DDA32B - Penstock & Stoplogs Schedules - Design Preparation to SO Approval	584	03-Jul-17 A	06-Feb-19					
Valves Schedules (DDA32C)		580	03-Jul-17 A	03-Feb-19					

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 31Jan19)			PAGE 3 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Jan	Feb	Mar	Apr	May
DG3222	DDA32C - Valves Schedules - Design Preparation to SO Approval	580	03-Jul-17 A	03-Feb-19			DDA32C - Valves Schedules - Design Preparation to SO Approval		
	Piping and Pipe Support Schedules (DDA32D)	580	03-Jul-17 A	03-Feb-19					
DG3864	DDA32D - Piping and Pipe Support Schedules - Design Preparation to SO Approval	580	03-Jul-17 A	03-Feb-19			DDA32D - Piping and Pipe Support Schedules - Design Preparation to SO Approval		
	Instrumentation Schedules (DDA32F)	592	03-Jul-17 A	14-Feb-19					
DG3234	DDA32F - Instrumentation Schedules - Design Preparation to SO Approval	592	03-Jul-17 A	14-Feb-19			DDA32F - Instrumentation Schedules - Design Preparation to SO Approval		
LOT #1 - Building / Facilities Design : CEPT+SF, PTW+IPS+SHB, UV, SDB+SSSB		801	22-Dec-16 A	02-Mar-19					
	Inlet Work, Preliminary Treatment Works, IPS and SHB	753	06-Feb-17 A	01-Mar-19					
	Civil and Structural Design (AIP5A / DDA5AB1B2)	753	06-Feb-17 A	01-Mar-19					
DB4830	DDA5B2 - SHB - C&S - Design Preparation to SO Approval	753	06-Feb-17 A	01-Mar-19			DDA5B2 - SHB - C&S - Design Preparation to SO Approval		
	Electrical and Mechanical Design (AIP9B / DDA5C1C2DEF)	695	01-Apr-17 A	25-Feb-19					
DB1264	DDA5C1-2 - PTW, IPS & SHB - (Super Structural Design) - GA Drawing - Design Preparation to SO Approval	695	01-Apr-17 A	25-Feb-19			DDA5C1-2 - PTW, IPS & SHB - (Super Structural Design) - GA Drawing - Design Preparation to SO Approval		
	UV Disinfection Facilities	792	22-Dec-16 A	22-Feb-19					
	Electrical and Mechanical Design (AIP7B / DDA7C1C2DEF)	792	22-Dec-16 A	22-Feb-19					
DB1352	DDA7C1-1 - UV Facilities - (Piling & Foundation Design) - GA Drawing - Design Preparation to SO Approval	792	22-Dec-16 A	22-Feb-19			DDA7C1-1 - UV Facilities - (Piling & Foundation Design) - GA Drawing - Design Preparation to SO Approval		
	Sludge Dewatering Building and Sludge Skip Storage Building	757	04-Feb-17 A	02-Mar-19					
	Civil and Structural Design (AIP8A / DDA8AB1B2)	757	04-Feb-17 A	02-Mar-19					
DB4858	DDA8B2 - SSSB - C&S - Design Preparation to SO Approval	757	04-Feb-17 A	02-Mar-19			DDA8B2 - SSSB - C&S - Design Preparation to SO Approval		
	Electrical and Mechanical Design (AIP9B / DDA8C1C2DEF)	670	29-Apr-17 A	27-Feb-19					
DB1476	DDA8C1-2 - SDB and SSSB - (Super Structural Design) - GA Drawing - Design Preparation to SO Approval	670	29-Apr-17 A	27-Feb-19			DDA8C1-2 - SDB and SSSB - (Super Structural Design) - GA Drawing - Design Preparation to SO Approval		
LOT #2 - Building / Facilities Design : AB+WS, DO, CB+EB4, FH		933	03-Oct-16 A	23-Apr-19					
	Administration Building & Maintenance Workshop	875	03-Oct-16 A	25-Feb-19					
	Electrical and Mechanical Design (AIP10B / DDA10C1C2DEF)	875	03-Oct-16 A	25-Feb-19					
DB2286	DDA10C1-1 - Admin Bldg. & Workshop (Piling & Foundation Design) - GA Drawing - Design Preparation to SO Approval	875	03-Oct-16 A	25-Feb-19			DDA10C1-1 - Admin Bldg. & Workshop (Piling & Foundation Design) - GA Drawing - Design Preparation to SO Approval		
	Deodorization Facilities No.1 and No.2	820	15-Dec-16 A	14-Mar-19					
	Civil and Structural Design (AIP9A / DDA9AB)	778	26-Jan-17 A	14-Mar-19					
DB2323	DDA9A - DO #1 & #2 (Architectural) - C&S - Design Preparation to SO Approval	766	26-Jan-17 A	02-Mar-19			DDA9A - DO #1 & #2 (Architectural) - C&S - Design Preparation to SO Approval		
DB5150	DDA9B - DO #1 & #2 (Structural) - C&S - Design Preparation to SO Approval	648	05-Jun-17 A	14-Mar-19			DDA9B - DO #1 & #2 (Structural) - C&S - Design Preparation to SO Approval		
	Electrical and Mechanical Design (AIP9B / DDA9C1C2DEF)	777	15-Dec-16 A	31-Jan-19					
DB2348	DDA9C1 - DO #1 & #2 - GA Drawing - Design Preparation to SO Approval	777	15-Dec-16 A	31-Jan-19			DDA9C1 - DO #1 & #2 - GA Drawing - Design Preparation to SO Approval		
	Street Fire Hydrant Pump Room & GENSET Room	868	07-Dec-16 A	23-Apr-19					
	Civil and Structural Design (AIP17A / DDA17AB)	689	23-Mar-17 A	09-Feb-19					
DB2423	DDA17A - FH Pump Room & GENSET Room (Architectural) - C&S - Design Preparation to SO Approval	689	23-Mar-17 A	09-Feb-19			DDA17A - FH Pump Room & GENSET Room (Architectural) - C&S - Design Preparation to SO Approval		
DB5220	DDA17B - FH Pump Room & GENSET Room (Structural) - C&S - Design Preparation to SO Approval	551	01-Aug-17 A	02-Feb-19			DDA17B - FH Pump Room & GENSET Room (Structural) - C&S - Design Preparation to SO Approval		
	Electrical and Mechanical Design (AIP17B / DDA17C1C2DEF)	868	07-Dec-16 A	23-Apr-19					
DB2448	DDA17C1 - FH Pump Room & GENSET Room - GA Drawing - Design Preparation to SO Approval	826	07-Dec-16 A	12-Mar-19			DDA17C1 - FH Pump Room & GENSET Room - GA Drawing - Design Preparation to SO Approval		
DB4648	DDA17D - FH Pump Room & GENSET Room - Electrical - Design Preparation to SO Approval	762	23-Mar-17 A	23-Apr-19				DDA17D - FH Pump Room & GENSET Room - Electrical - Design Preparation to SO Approval	
LOT #3 - Building / Facilities Design : EB1, EB2, EB3, EB4, RW, DG+ICW, Inlet/Outlet Connection		917	16-Sep-16 A	21-Mar-19					
	Electrical Building No.1, No.2, No.3, No.4	915	16-Sep-16 A	19-Mar-19					
	Civil and Structural Design for EB123 (AIP13A / DDA13AB)	699	08-Apr-17 A	07-Mar-19					
DB3123	DDA13A - EB1, EB2 and EB3 - C&S - Design Preparation to SO Approval	699	08-Apr-17 A	07-Mar-19			DDA13A - EB1, EB2 and EB3 - C&S - Design Preparation to SO Approval		
	Electrical and Mechanical Design for EB1234 (AIP13B / DDA13C1C2DEF)	915	16-Sep-16 A	19-Mar-19					
DB3148	DDA13C1 - EB1, EB2, EB3 & EB4 - GA Drawing - Design Preparation to SO Approval	915	16-Sep-16 A	19-Mar-19			DDA13C1 - EB1, EB2, EB3 & EB4 - GA Drawing - Design Preparation to SO Approval		
	ICW and DG Store & Chemical Waste Storage Building	836	30-Nov-16 A	16-Mar-19					
	Civil and Structural Design (AIP16A / DDA16AB)	501	16-Oct-17 A	01-Mar-19					
DB3323	DDA16A - ICW, DG & Chemical Stores - C&S - Design Preparation to SO Approval	501	16-Oct-17 A	01-Mar-19			DDA16A - ICW, DG & Chemical Stores - C&S - Design Preparation to SO Approval		
	Electrical and Mechanical Design (AIP16B / DDA16C1C2D)	836	30-Nov-16 A	16-Mar-19					

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 31Jan19)			PAGE 4 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Jan	Feb	Mar	Apr	May
DB3348	DDA16C1 - ICW, DG & Chemical Stores - GA Drawing - Design Preparation to SO Approval	836	30-Nov-16 A	16-Mar-19					
DB4694	DDA16D - ICW, DG & Chemical Stores - Building Services - Design Preparation to SO Approval	660	24-May-17 A	15-Mar-19					
Inlet & Outlet Pipe Connections and Diversion Pipeworks		713	08-Apr-17 A	21-Mar-19					
Civil and Structural Design (AIP11 / DDA11ABC)		713	08-Apr-17 A	21-Mar-19					
DB3438	DDA11B - C&S Detailed Design Report for Inlet Connections Pipework - Design Preparation to SO Approval	713	08-Apr-17 A	21-Mar-19					
LOT #4 - Building / Facilities Design : GH, PF		688	24-Apr-17 A	12-Mar-19					
Gatehouse		688	24-Apr-17 A	12-Mar-19					
Civil and Structural Design (AIP18A / DDA18AB)		603	18-Jul-17 A	12-Mar-19					
DB4434	DDA18A - Gatehouse - C&S - Design Preparation to SO Approval	603	18-Jul-17 A	12-Mar-19					
Electrical and Mechanical Design (AIP18B / DDA18C)		686	24-Apr-17 A	11-Mar-19					
DB4754	DDA18C - Gatehouse - Building Services - Design Preparation to SO Approval	686	24-Apr-17 A	11-Mar-19					
Civil & Structural Works		894	04-Oct-17 A	15-Mar-20					
LOT #1 - Bldg / Facilities Const. (Arch'l & Struct'l) : CEPT+SF, PTW+IPS+SHB, UV, SDB+SSSB		592	07-Oct-17 A	21-May-19					
Chemically Enhanced Primary Treatment (CEPT)		454	22-Feb-18 A	21-May-19					
CS1526	Backfilling (except in Water Tightness Test area)	292	28-Apr-18 A	14-Feb-19					
CS1530	Superstructure (rc and metalworks)	454	22-Feb-18 A	21-May-19					
CS1534	Water Tightness Test + Backfilling	60	10-Feb-19	11-Apr-19					
CS1540	Internal ABWF - CEPT	80	09-Feb-19	30-Apr-19					
System Control Flowmeter Chamber (SF)		68	02-Mar-19	09-May-19					
CS1400	Substructure (rc structure)	40	02-Mar-19	11-Apr-19					
CS1405	Backfilling	5	06-Apr-19	11-Apr-19					
CS1410	Superstructure (rc and metalworks)	19	06-Apr-19	25-Apr-19					
CS1420	ABWF - System Control Flowmeter Chamber	14	25-Apr-19	09-May-19					
Inlet Work, Preliminary Treatment Works and Inlet Pumping Station (PTW & IPS)		196	27-Oct-18 A	10-May-19					
CS1220	Substructure (rc structure)	152	27-Oct-18 A	28-Mar-19					
CS1224	Removal of ELS	3	28-Mar-19	31-Mar-19					
CS1226	Backfilling (except in Water Tightness Test area)	2	09-Mar-19	11-Mar-19					
CS1230	Superstructure (rc and metalworks)	93	11-Jan-19 A	13-Apr-19					
CS1235	Water Tightness Test + Backfilling	93	07-Feb-19	10-May-19					
Solid Handling Building (SHB)		546	22-Oct-17 A	20-Apr-19					
CS1300	Substructure (rc structure)	508	22-Oct-17 A	13-Mar-19					
CS1305	Backfilling (except in Water Tightness Test area)	6	11-Apr-19	16-Apr-19					
CS1310	Superstructure (rc and metalworks)	29	14-Mar-19	11-Apr-19					
CS1315	Water Tightness Test + Backfilling	29	14-Mar-19	11-Apr-19					
CS1320	ABWF - Solid Handling Building	13	08-Apr-19	20-Apr-19					
UV Disinfection Facility (UV)		545	07-Oct-17 A	04-Apr-19					
CS1910	Substructure (rc structure)	485	07-Oct-17 A	03-Feb-19					
CS1915	Backfilling (except in Water Tightness Test area)	49	01-Jan-19 A	18-Feb-19					
CS1920	Superstructure (rc and metalworks)	99	01-Dec-18 A	09-Mar-19					
CS1925	Water Tightness Test + Backfilling	26	02-Mar-19	28-Mar-19					
CS1930	ABWF - UV Disinfection Facility	48	15-Feb-19	04-Apr-19					
Sludge Dewatering Building (SDB)		118	27-Nov-18 A	25-Mar-19					
CS1845	Water Tightness Test + Backfilling	81	02-Jan-19 A	23-Mar-19					
CS1850	ABWF - Sludge Dewatering Building	118	27-Nov-18 A	25-Mar-19					
Sludge Skip Storage Building (SSSB)		564	22-Oct-17 A	08-May-19					
CS2900	Substructure (rc structure)	532	22-Oct-17 A	06-Apr-19					

DATA DATE: 31-Jan-19			LAYOUT: SW Project Phase 1 Rev 10 (3M 31Jan19)			PAGE 5 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	Jan	Feb	Mar	Apr	May	
CS2905	Backfilling	2	06-Apr-19	08-Apr-19				Backfilling		
CS2910	Superstructure (rc and metalworks)	32	06-Apr-19	08-May-19				Superstructure (rc and metalworks)		
LOT #2 - Bldg / Facilities Const. (Arch'l & Struct'l) : AB+WS, DO, CB, FH			584	13-Oct-17 A	19-May-19					
Administration Building & Maintenance Workshop (AB & WS)			77	21-Dec-18 A	07-Mar-19					
CS1125	Water Tightness Test	42	18-Jan-19 A	28-Feb-19				Water Tightness Test		
CS1130	ABWF - Administration Building & Maintenance Workshop	77	21-Dec-18 A	07-Mar-19				ABWF - Administration Building & Maintenance Workshop		
Deodorization Facilities No. 1 (DO 1)			551	19-Oct-17 A	23-Apr-19					
CS1610	Substructure (rc structure)	522	19-Oct-17 A	25-Mar-19				Substructure (rc structure)		
CS1615	Backfilling	3	25-Mar-19	28-Mar-19				Backfilling		
CS1620	Superstructure (rc and metalworks)	15	25-Mar-19	09-Apr-19				Superstructure (rc and metalworks)		
CS1630	ABWF - Deodorization Facilities No.1	14	09-Apr-19	23-Apr-19				ABWF - Deodorization Facilities No.1		
Deodorization Facilities No. 2 (DO 2)			556	22-Oct-17 A	30-Apr-19					
CS1710	Substructure (rc structure)	530	22-Oct-17 A	04-Apr-19				Substructure (rc structure)		
CS1715	Backfilling	3	05-Apr-19	07-Apr-19				Backfilling		
CS1720	Superstructure (rc and metalworks)	12	05-Apr-19	16-Apr-19				Superstructure (rc and metalworks)		
CS1730	ABWF - Deodorization Facilities No.2	14	17-Apr-19	30-Apr-19				ABWF - Deodorization Facilities No.2		
Chemical Building (CB)			562	13-Oct-17 A	27-Apr-19					
CS2310	Substructure (rc structure)	500	13-Oct-17 A	24-Feb-19				Substructure (rc structure)		
CS2315	Backfilling	2	24-Feb-19	26-Feb-19				Backfilling		
CS2320	Superstructure (rc and metalworks)	39	26-Feb-19	06-Apr-19				Superstructure (rc and metalworks)		
CS2330	ABWF - Chemical Building	24	03-Apr-19	27-Apr-19				ABWF - Chemical Building		
Street Fire Hydrant Pump Room & GENSET Room (FH)			72	08-Mar-19	19-May-19					
CS3010	Substructure (rc structure)	30	08-Mar-19	07-Apr-19				Substructure (rc structure)		
CS3015	Backfilling	2	07-Apr-19	09-Apr-19				Backfilling		
CS3020	Superstructure (rc and metalworks)	42	07-Apr-19	19-May-19				Superstructure (rc and metalworks)		
LOT #3 - Bldg / Facilities Const. (Arch'l & Struct'l) : EB, RW, DG, ICW, JC			587	04-Oct-17 A	13-May-19					
Electrical Building No.1 (EB1)			549	22-Oct-17 A	23-Apr-19					
CS2410	Substructure (rc structure)	503	22-Oct-17 A	08-Mar-19				Substructure (rc structure)		
CS2415	Backfilling	7	08-Mar-19	15-Mar-19				Backfilling		
CS2420	Superstructure (rc and metalworks)	33	08-Mar-19	10-Apr-19				Superstructure (rc and metalworks)		
CS2430	ABWF - Electrical Building No.1	19	04-Apr-19	23-Apr-19				ABWF - Electrical Building No.1		
Electrical Building No.2 (EB2)			66	02-Feb-19	09-Apr-19					
CS2510	Substructure (rc structure)	23	02-Feb-19	25-Feb-19				Substructure (rc structure)		
CS2515	Backfilling	4	31-Mar-19	04-Apr-19				Backfilling		
CS2520	Superstructure (rc and metalworks)	34	25-Feb-19	31-Mar-19				Superstructure (rc and metalworks)		
CS2530	ABWF - Electrical Building No.2	14	26-Mar-19	09-Apr-19				ABWF - Electrical Building No.2		
Electrical Building No.3 (EB3)			549	04-Oct-17 A	05-Apr-19					
CS2610	Substructure (rc structure)	507	04-Oct-17 A	22-Feb-19				Substructure (rc structure)		
CS2615	Backfilling	6	19-Mar-19	25-Mar-19				Backfilling		
CS2620	Superstructure (rc and metalworks)	32	18-Feb-19	22-Mar-19				Superstructure (rc and metalworks)		
CS2630	ABWF - Electrical Building No.3	17	19-Mar-19	05-Apr-19				ABWF - Electrical Building No.3		
Electrical Building No.4 (EB4)			502	22-Oct-17 A	08-Mar-19					
CS2710	Substructure (rc structure)	495	22-Oct-17 A	01-Mar-19				Substructure (rc structure)		
CS2715	Backfilling	13	19-Feb-19	04-Mar-19				Backfilling		
CS2720	Superstructure (rc and metalworks)	38	24-Jan-19 A	02-Mar-19				Superstructure (rc and metalworks)		
CS2730	ABWF - Electrical Building No.4	17	19-Feb-19	08-Mar-19				ABWF - Electrical Building No.4		

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 31-Jan-19)			PAGE 6 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	Jan	Feb	Mar	Apr	May
Re-use Water Building (RW)									
CS2010	Substructure (rc structure)	94	08-Feb-19	13-May-19					
CS2015	Backfilling (except in Water Tightness Test area)	26	08-Feb-19	06-Mar-19					
CS2020	Superstructure (rc and metalworks)	2	06-Mar-19	08-Mar-19					
CS2025	Water Tightness Test + Backfilling	52	06-Mar-19	27-Apr-19					
CS2030	ABWF - Re-use Water Building	24	19-Apr-19	13-May-19					
DG Store & Chemical Waste Storage Building (DG) and Irrigation & Cleansing Water Pump Room (ICW)									
CS2800	Substructure (rc structure)	553	22-Oct-17 A	28-Apr-19					
CS2805	Backfilling	520	22-Oct-17 A	26-Mar-19					
CS2810	Superstructure (rc and metalworks)	3	26-Mar-19	29-Mar-19					
CS2820	ABWF - DG Store and Chemical Waste Storage Building / Irrigation and Cleansing Water Pump Room	36	16-Mar-19	21-Apr-19					
Existing Junction Chamber (JC)									
CS2210	Bar Screen Installation	243	12-Jun-18 A	09-Feb-19					
LOT #4 - Bldg / Facilities Const. (Arch'l & Struct'l) : GH, PF, FW									
Gatehouse (GH)									
CS3100	Substructure (rc structure)	56	01-Apr-19	26-May-19					
Payment Flowmeter Chamber (PF)									
CS2100	Substructure (rc structure)	128	12-Dec-18 A	18-Apr-19					
CS2105	Water Tightness Test + Backfilling	61	12-Dec-18 A	10-Feb-19					
CS2110	Superstructure (rc and metalworks)	54	09-Feb-19	04-Apr-19					
CS2120	ABWF - Payment Flowmeter Chamber	31	28-Jan-19 A	27-Feb-19					
Foul Water Pump Sump (FW)									
CS3396	Substructure (rc structure)	43	07-Mar-19	18-Apr-19					
External Works & Miscellaneous									
CS3200	Site Formation along Boundary Wall (Perimeter)	57	26-Mar-19	21-May-19					
CS3201	Slope works and Retaining Wall (Eastern Portion)	57	26-Mar-19	21-May-19					
CS3203	Slope works and Retaining Wall (Northern Portion)	626	29-Jun-18 A	15-Mar-20					
CS3210	Drainage Inlet connection (Diversion of Three Existing Sewage Rising Mains) incl. slope & retaining wall work @ P8	180	12-Feb-19	10-Aug-19					
CS3225	Drainage Outlet connection to the Existing Stormwater Drainage System along Ha Tsuen Road	320	04-Jul-18 A	19-May-19					
CS3230	CLP Cable Duct and Draw Pits (within the Site)	320	04-Jul-18 A	19-May-19					
CS3250	EVA (Road & Drainage)	120	12-Feb-19	11-Jun-19					
CS3252	RC Trench and Odour Pipe (DO1, DO2)	92	20-Feb-19	22-May-19					
CS3254	Process Pipe	100	31-Jan-19	10-May-19					
CS3256	Drainage Pipe (Stormwater) incl. Surface Drainage at Site Platform & On Slope	626	29-Jun-18 A	15-Mar-20					
CS3258	Emergency By-Pass Pipe	121	31-Jan-19	31-May-19					
CS3260	Sewage Pipe	121	08-Feb-19	08-Jun-19					
CS3262	Cable Duct and Draw Pits	121	16-Feb-19	16-Jun-19					
CS3276	WSD External Watermain Laying Works	383	15-Jul-18 A	01-Aug-19					
CS3278	Internal Watermain Laying Works	225	14-Dec-18 A	26-Jul-19					
Green Roof									
CS3340	Administration Building and Maintenance Workshop	180	31-Jan-19	29-Jul-19					
CS3350	Sludge Dewatering Building	180	11-Feb-19	09-Aug-19					
CS3360	Chemical Building	150	11-Feb-19	10-Jul-19					
Statutory Works									
Electrical Supply & Energization - CLP									
SR100	Enabling Works for Handover of EB1 Transformer Rooms to CLP	247	21-Feb-19	25-Oct-19					

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 31-Jan-19)			PAGE 7 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	Jan	Feb	Mar	Apr	May
SR110	LV Switchboard Installation & Cabling Works in EB1 Switch Rooms	55	23-Apr-19	17-Jun-19					
SR115	Enabling Works for Handover of EB3 Transformer Room to CLP	40	05-Apr-19	15-May-19					
SR125	LV Switchboard Installation & Cabling Works in EB3 Switch Room	60	18-Apr-19	17-Jun-19					
SR140	CLP Internal Cabling Works	80	21-Feb-19	11-May-19					
Fire Services - FSD		185	23-Apr-19	25-Oct-19					
SR300	FS Pump Room & Tank Installation (FH)	185	23-Apr-19	25-Oct-19					
E&M Works		1099	27-Nov-16 A	30-Nov-19					
Procurement		949	27-Nov-16 A	03-Jul-19					
Chemically Enhanced Primary Treatment (CEPT)		560	10-Nov-17 A	24-May-19					
EM3112	Manufacturing & Logistic (Major Equipment)	360	21-Feb-18 A	16-Feb-19					
EM3114	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	460	10-Nov-17 A	12-Feb-19					
EM3116	Manufacturing & Logistic (Penstock, Pipe & Valve)	176	29-Nov-18 A	24-May-19					
EM3118	CMS Preparation, Submission & Approval (Electrical)	460	10-Nov-17 A	12-Feb-19					
EM3120	Manufacturing & Logistic (Electrical)	176	29-Nov-18 A	24-May-19					
EM3122	CMS Preparation, Submission & Approval (Building Services)	462	10-Nov-17 A	14-Feb-19					
EM3124	Manufacturing & Logistic (Building Services)	164	29-Nov-18 A	11-May-19					
System Control Flowmeter Chamber (SF)		555	10-Nov-17 A	18-May-19					
EM3134	Manufacturing & Logistic (Major Equipment)	228	28-Sep-18 A	14-May-19					
EM3136	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	462	10-Nov-17 A	14-Feb-19					
EM3138	Manufacturing & Logistic (Penstock, Pipe & Valve)	95	29-Nov-18 A	03-Mar-19					
EM3140	CMS Preparation, Submission & Approval (Electrical)	462	10-Nov-17 A	14-Feb-19					
EM3142	Manufacturing & Logistic (Electrical)	139	29-Nov-18 A	16-Apr-19					
EM3144	CMS Preparation, Submission & Approval (Building Services)	462	10-Nov-17 A	14-Feb-19					
EM3146	Manufacturing & Logistic (Building Services)	171	29-Nov-18 A	18-May-19					
Inlet Work, Preliminary Treatment Units and Inlet Pumping Station (PTW & IPS)		880	04-Jan-17 A	02-Jun-19					
EM3135	CMS Preparation, Submission & Approval (Major Equipment)	761	04-Jan-17 A	04-Feb-19					
EM3137	Manufacturing & Logistic (Major Equipment)	175	10-Dec-18 A	02-Jun-19					
EM3141	Witness FAT - Main Sewage Pumps	28	05-Feb-19	04-Mar-19					
EM3635	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	491	01-Oct-17 A	04-Feb-19					
EM3645	Manufacturing & Logistic (Penstock, Pipe & Valve)	171	11-Dec-18 A	31-May-19					
EM3655	CMS Preparation, Submission & Approval (Electrical)	492	01-Oct-17 A	05-Feb-19					
EM3665	Manufacturing & Logistic (Electrical)	135	05-Dec-18 A	19-Apr-19					
EM3675	CMS Preparation, Submission & Approval (Building Services)	493	01-Oct-17 A	06-Feb-19					
EM3685	Manufacturing & Logistic (Building Services)	174	02-Dec-18 A	24-May-19					
Solid Handling Building (SHB)		773	12-Apr-17 A	24-May-19					
EM3145	CMS Preparation, Submission & Approval (Major Equipment)	662	12-Apr-17 A	02-Feb-19					
EM3150	Manufacturing & Logistic (Major Equipment)	124	11-Nov-18 A	15-Mar-19					
EM3695	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	491	01-Oct-17 A	04-Feb-19					
EM3705	Manufacturing & Logistic (Penstock, Pipe & Valve)	113	11-Nov-18 A	03-Mar-19					
EM3715	CMS Preparation, Submission & Approval (Electrical)	490	01-Oct-17 A	03-Feb-19					
EM3725	Manufacturing & Logistic (Electrical)	130	10-Dec-18 A	19-Apr-19					
EM3735	CMS Preparation, Submission & Approval (Building Services)	491	01-Oct-17 A	04-Feb-19					
EM3745	Manufacturing & Logistic (Building Services)	166	10-Dec-18 A	24-May-19					
UV Disinfection Facility (UV)		578	21-Nov-17 A	22-Jun-19					
EM3190	Manufacturing & Logistic (Major Equipment)	351	30-Apr-18 A	16-Apr-19					
EM3192	Delivery To Site (Major Equipment)	141	10-Dec-18 A	30-Apr-19					
EM3755	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	442	21-Nov-17 A	05-Feb-19					

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 31-Jan-19)			PAGE 8 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	Jan	Feb	Mar	Apr	May
EM3765	Manufacturing & Logistic (Penstock, Pipe & Valve)	192	12-Dec-18 A	22-Jun-19					
EM3775	CMS Preparation, Submission & Approval (Electrical)	442	21-Nov-17 A	05-Feb-19					
EM3785	Manufacturing & Logistic (Electrical)	129	12-Dec-18 A	20-Apr-19					
EM3795	CMS Preparation, Submission & Approval (Building Services)	454	21-Nov-17 A	18-Feb-19					
EM3805	Manufacturing & Logistic (Building Services)	120	18-Feb-19	18-Jun-19					
Sludge Dewatering Building (SDB)		940	27-Nov-16 A	25-Jun-19					
EM3175	CMS Preparation, Submission & Approval (Major Equipment)	812	27-Nov-16 A	16-Feb-19					
EM3180	Manufacturing & Logistic (Major Equipment)	241	27-Oct-18 A	25-Jun-19					
EM3815	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	478	27-Oct-17 A	16-Feb-19					
EM3825	Manufacturing & Logistic (Penstock, Pipe & Valve)	126	17-Feb-19	22-Jun-19					
EM3835	CMS Preparation, Submission & Approval (Electrical)	464	27-Oct-17 A	02-Feb-19					
EM3845	Manufacturing & Logistic (Electrical)	106	29-Nov-18 A	14-Mar-19					
EM3855	CMS Preparation, Submission & Approval (Building Services)	483	27-Oct-17 A	21-Feb-19					
EM3865	Manufacturing & Logistic (Building Services)	120	21-Feb-19	21-Jun-19					
Sludge Skip Storage Building (SSSB)		557	04-Sep-17 A	14-Mar-19					
EM3875	CMS Preparation, Submission & Approval (Electrical)	514	04-Sep-17 A	31-Jan-19					
EM3885	Manufacturing & Logistic (Electrical)	106	29-Nov-18 A	14-Mar-19					
EM3895	CMS Preparation, Submission & Approval (Building Services)	514	04-Sep-17 A	31-Jan-19					
EM3905	Manufacturing & Logistic (Building Services)	94	29-Nov-18 A	02-Mar-19					
Administration Building & Maintenance Workshop (AB & WS)		810	31-Jan-17 A	20-Apr-19					
EM3125	CMS Preparation, Submission & Approval (Major Equipment)	742	31-Jan-17 A	11-Feb-19					
EM3130	Manufacturing & Logistic (Major Equipment)	129	29-Nov-18 A	06-Apr-19					
EM3915	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	532	30-Aug-17 A	12-Feb-19					
EM3925	Manufacturing & Logistic (Penstock, Pipe & Valve)	115	29-Nov-18 A	23-Mar-19					
EM3935	CMS Preparation, Submission & Approval (Electrical)	532	30-Aug-17 A	12-Feb-19					
EM3945	Manufacturing & Logistic (Electrical)	143	29-Nov-18 A	20-Apr-19					
EM3955	CMS Preparation, Submission & Approval (Building Services)	532	30-Aug-17 A	12-Feb-19					
EM3965	Manufacturing & Logistic (Building Services)	143	29-Nov-18 A	20-Apr-19					
Deodorization Facilities No. 1 & 2 (DO 1 & DO 2)		905	10-Jan-17 A	03-Jul-19					
EM3165	CMS Preparation, Submission & Approval (Major Equipment)	762	10-Jan-17 A	10-Feb-19					
EM3170	Manufacturing & Logistic (Major Equipment)	95	27-Nov-18 A	01-Mar-19					
EM3171	Witness FAT - DO 1 & DO 2	78	27-Nov-18 A	13-Feb-19					
EM3172	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	532	30-Aug-17 A	12-Feb-19					
EM3173	Manufacturing & Logistic (Penstock, Pipe & Valve)	142	27-Nov-18 A	17-Apr-19					
EM3975	CMS Preparation, Submission & Approval (Electrical)	532	30-Aug-17 A	12-Feb-19					
EM3985	Manufacturing & Logistic (Electrical)	114	27-Nov-18 A	20-Mar-19					
EM3995	CMS Preparation, Submission & Approval (Building Services)	553	30-Aug-17 A	05-Mar-19					
EM4005	Manufacturing & Logistic (Building Services)	120	05-Mar-19	03-Jul-19					
Chemical Building (CB)		530	08-Nov-17 A	21-Apr-19					
EM3230	Manufacturing & Logistic (Major Equipment)	329	17-Mar-18 A	08-Feb-19					
EM4015	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	454	08-Nov-17 A	05-Feb-19					
EM4025	Manufacturing & Logistic (Penstock, Pipe & Valve)	84	12-Dec-18 A	06-Mar-19					
EM4035	CMS Preparation, Submission & Approval (Electrical)	452	08-Nov-17 A	03-Feb-19					
EM4045	Manufacturing & Logistic (Electrical)	109	12-Dec-18 A	30-Mar-19					
EM4055	CMS Preparation, Submission & Approval (Building Services)	453	08-Nov-17 A	04-Feb-19					
EM4065	Manufacturing & Logistic (Building Services)	131	12-Dec-18 A	21-Apr-19					
Street Fire Hydrant Pump Room & GENSET Room (FH)		764	23-Mar-17 A	25-Apr-19					

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 31Jan19)			PAGE 9 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	Jan	Feb	Mar	Apr	May
EM3275	CMS Preparation, Submission & Approval (Major Equipment)	684	23-Mar-17 A	04-Feb-19					
EM3280	Manufacturing & Logistic (Major Equipment)	95	12-Dec-18 A	16-Mar-19					
EM4075	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	491	01-Oct-17 A	03-Feb-19					
EM4085	Manufacturing & Logistic (Penstock, Pipe & Valve)	135	12-Dec-18 A	25-Apr-19					
EM4095	CMS Preparation, Submission & Approval (Electrical)	493	01-Oct-17 A	05-Feb-19					
EM4105	Manufacturing & Logistic (Electrical)	111	12-Dec-18 A	01-Apr-19					
EM4115	CMS Preparation, Submission & Approval (Building Services)	499	01-Oct-17 A	12-Feb-19					
EM4125	Manufacturing & Logistic (Building Services)	122	12-Dec-18 A	12-Apr-19					
Electrical Buildings (EB1, EB2, EB3 & EB4)		779	23-Feb-17 A	13-Apr-19					
EM3235	CMS Preparation, Submission & Approval (Major Equipment)	711	23-Feb-17 A	03-Feb-19					
EM3240	Manufacturing & Logistic (Major Equipment)	103	08-Dec-18 A	20-Mar-19					
EM3245	Witness FAT - LV Switchboards (8 nos. for EB's and 4 nos. for SDB)	21	31-Jan-19	20-Feb-19					
EM3300	CMS Preparation, Submission & Approval (Electrical)	510	11-Sep-17 A	03-Feb-19					
EM3305	Manufacturing & Logistic (Electrical)	110	08-Dec-18 A	28-Mar-19					
EM3310	CMS Preparation, Submission & Approval (Control & Instrument)	512	11-Sep-17 A	05-Feb-19					
EM3315	Manufacturing & Logistic (Control & Instrument)	115	08-Dec-18 A	01-Apr-19					
EM3320	CMS Preparation, Submission & Approval (Building Services)	541	09-Aug-17 A	31-Jan-19					
EM3325	Manufacturing & Logistic (Building Services)	126	08-Dec-18 A	13-Apr-19					
Re-use Water Building (RW)		512	19-Nov-17 A	14-Apr-19					
EM3200	Manufacturing & Logistic (Major Equipment)	237	28-Jun-18 A	19-Feb-19					
EM4135	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	441	19-Nov-17 A	03-Feb-19					
EM4145	Manufacturing & Logistic (Penstock, Pipe & Valve)	106	15-Nov-18 A	28-Feb-19					
EM4155	CMS Preparation, Submission & Approval (Electrical)	440	19-Nov-17 A	02-Feb-19					
EM4165	Manufacturing & Logistic (Electrical)	111	12-Dec-18 A	01-Apr-19					
EM4175	CMS Preparation, Submission & Approval (Building Services)	442	19-Nov-17 A	03-Feb-19					
EM4185	Manufacturing & Logistic (Building Services)	124	12-Dec-18 A	14-Apr-19					
DG Store & Chemical Waste Storage Building (DG) and Irrigation & Cleansing Water Pump Room (ICW)		691	24-May-17 A	14-Apr-19					
EM3255	CMS Preparation, Submission & Approval (Major Equipment)	620	24-May-17 A	02-Feb-19					
EM3260	Manufacturing & Logistic (Major Equipment)	111	12-Dec-18 A	01-Apr-19					
EM4195	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	423	10-Dec-17 A	05-Feb-19					
EM4205	Manufacturing & Logistic (Penstock, Pipe & Valve)	79	12-Dec-18 A	28-Feb-19					
EM4215	CMS Preparation, Submission & Approval (Electrical)	490	30-Sep-17 A	02-Feb-19					
EM4225	Manufacturing & Logistic (Electrical)	86	12-Dec-18 A	07-Mar-19					
EM4235	CMS Preparation, Submission & Approval (Building Services)	492	30-Sep-17 A	03-Feb-19					
EM4245	Manufacturing & Logistic (Building Services)	124	12-Dec-18 A	14-Apr-19					
Gatehouse (GH)		741	24-Apr-17 A	05-May-19					
EM3285	CMS Preparation, Submission & Approval (Building Services)	653	24-Apr-17 A	05-Feb-19					
EM3290	Manufacturing & Logistic (Building Services)	144	12-Dec-18 A	05-May-19					
Payment Flowmeter Chamber (PF)		630	01-Sep-17 A	23-May-19					
EM3210	Manufacturing & Logistic (Major Equipment)	182	28-Sep-18 A	29-Mar-19					
EM3211	Witness FAT - Payment Flowmeter and Reference Flowmeter	7	31-Jan-19	06-Feb-19					
EM4255	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	520	01-Sep-17 A	02-Feb-19					
EM4265	Manufacturing & Logistic (Penstock, Pipe & Valve)	113	11-Dec-18 A	03-Apr-19					
EM4275	CMS Preparation, Submission & Approval (Electrical)	439	20-Nov-17 A	01-Feb-19					
EM4285	Manufacturing & Logistic (Electrical)	117	02-Dec-18 A	28-Mar-19					
EM4295	CMS Preparation, Submission & Approval (Building Services)	452	20-Nov-17 A	14-Feb-19					
EM4305	Manufacturing & Logistic (Building Services)	98	14-Feb-19	23-May-19					

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M31Jan19)			PAGE 10 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	Jan	Feb	Mar	Apr	May
SCADA and CMMS Systems									
EM3330	CMS Preparation, Submission & Approval	695	01-Jul-17 A	27-May-19					
EM3335	Manufacturing & Logistic (SCADA)	581	01-Jul-17 A	02-Feb-19					
EM3340	Witness FAT - SCADA System	125	12-Dec-18 A	15-Apr-19					
EM3345	Manufacturing & Logistic (CMMS)	28	31-Jan-19	27-Feb-19					
EM3350	Witness FAT - CMMS	112	04-Feb-19	27-May-19					
EM3350	Witness FAT - CMMS	14	17-Feb-19	03-Mar-19					
Installation									
Chemically Enhanced Primary Treatment (CEPT)									
EM1500	Plant (Mechanical) Installation	304	31-Jan-19	30-Nov-19					
EM1505	Pipeworks	176	18-Feb-19	13-Aug-19					
EM1510	Electrical Installation	142	18-Feb-19	10-Jul-19					
EM1515	Cabling Works	120	15-Apr-19	13-Aug-19					
EM1525	BS - MVAC Installation	75	15-Apr-19	29-Jun-19					
EM1535	BS - Plumbing and Drainage Installation	120	15-Apr-19	13-Aug-19					
Solid Handling Building (SHB)									
EM1300	Plant (Mechanical) Installation	90	21-Apr-19	19-Jul-19					
UV Disinfection Facility (UV)									
EM1900	Plant (Mechanical) Installation	240	04-Apr-19	30-Nov-19					
Sludge Dewatering Building (SDB)									
EM1800	Plant (Mechanical) Installation	210	28-Feb-19	26-Sep-19					
EM1810	Electrical Installation	70	04-Apr-19	13-Jun-19					
Administration Building & Maintenance Workshop (AB & WS)									
EM1100	SCADA System	253	31-Jan-19	10-Oct-19					
EM1105	Plant Installation (WS)	180	31-Jan-19	29-Jul-19					
EM1110	ELV System	180	31-Jan-19	29-Jul-19					
EM1120	BS - MVAC Installation	180	31-Jan-19	29-Jul-19					
EM1130	Passenger Lift	180	28-Feb-19	26-Aug-19					
EM1140	BS - FS System & Control	180	15-Mar-19	10-Sep-19					
EM1145	BS - Electrical	180	14-Apr-19	10-Oct-19					
Deodorization Facilities No. 1 (DO 1)									
EM1600	Plant (Mechanical) Installation	90	23-Apr-19	22-Jul-19					
Chemical Building (CB)									
EM2300	Plant (Mechanical) Installation	120	27-Apr-19	25-Aug-19					
Electrical Building No.1 (EB1)									
EM2400	Electrical Installation	90	23-Apr-19	22-Jul-19					
EM2425	BS - MVAC Installation	75	23-Apr-19	07-Jul-19					
Electrical Building No.2 (EB2)									
EM2500	Electrical Installation	110	09-Apr-19	28-Jul-19					
EM2510	Cabling Works	90	09-Apr-19	08-Jul-19					
EM2520	BS - Electrical	60	24-Apr-19	23-Jun-19					
EM2525	BS - MVAC Installation	75	09-Apr-19	23-Jun-19					
EM2530	BS - FS Installation	60	24-Apr-19	23-Jun-19					
EM2535	BS - Plumbing and Drainage Installation	60	24-Apr-19	23-Jun-19					
Electrical Building No.3 (EB3)									
EM2600	Electrical Installation	106	05-Apr-19	20-Jul-19					
EM2610	Cabling Works	90	16-Apr-19	15-Jul-19					

DATA DATE: 31-Jan-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 31Jan19)			PAGE 11 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Jan	Feb	Mar	Apr	May
EM2620	BS - Electrical	60	21-Apr-19	20-Jun-19					
EM2625	BS - MVAC Installation	75	05-Apr-19	19-Jun-19					
EM2630	BS - FS Installation	60	21-Apr-19	20-Jun-19					
EM2635	BS - Plumbing and Drainage Installation	60	21-Apr-19	20-Jun-19					
Electrical Building No.4 (EB4)		121	07-Mar-19	06-Jul-19					
EM3400	Electrical Installation	90	08-Mar-19	06-Jun-19					
EM3410	Cabling Works	90	07-Apr-19	06-Jul-19					
EM3420	BS - Electrical	60	23-Mar-19	22-May-19					
EM3425	BS - MVAC Installation	75	07-Mar-19	21-May-19					
EM3430	BS - FS Installation	60	23-Mar-19	22-May-19					
EM3435	BS - Plumbing and Drainage Installation	60	23-Mar-19	22-May-19					
DG Store & Chemical Waste Storage Building (DG) and Irrigation & Cleansing Water Pump Room (ICW)		90	28-Apr-19	27-Jul-19					
EM3450	Plant (Mechanical) Installation	90	28-Apr-19	27-Jul-19					
Payment Flowmeter Chamber (PF)		120	19-Apr-19	17-Aug-19					
EM2100	Plant (Mechanical) Installation	120	19-Apr-19	17-Aug-19					
EM2105	Pipeworks	120	19-Apr-19	17-Aug-19					
Testing & Commissioning		313	03-Jun-18 A	11-Apr-19					
TC030	Operation Plan - Preparation for Submission	243	03-Jun-18 A	31-Jan-19					
TC035	Operation Plan - Submission to SO for Review and Approval	70	31-Jan-19	11-Apr-19					
TC040	Asset Management Plan - Preparation for Submission	243	03-Jun-18 A	31-Jan-19					
TC045	Asset Management Plan - Submission to SO for Review and Approval	70	31-Jan-19	11-Apr-19					

Appendix D1

Calibration Certificates for Impact Air Quality Monitoring Equipment

Summary of Calibration Certificates for TSP Monitoring Equipment used in this reporting month

Equip No.	Model	Serial No.	Calib Date	Due Date
ET/EA/001/05	Sibata LD-3B	8X4282	18/10/2018	17/04/2019
ET/EA/001/06	Sibata LD-3B	14746	15/10/2018	14/04/2019
ET/EA/001/08	Sibata LD-3B	135261	22/09/2018	21/03/2019
ET/EA/001/10	Sibata LD-3B	1Z5635	15/10/2018	14/04/2019
ET/EA/001/11	Sibata LD-3B	255863	16/11/2018	15/05/2019
ET/EA/001/13	Sibata LD-5	4Y1613	20/12/2018	19/06/2019
ET/EA/001/14	Sibata LD-3B	597340	07/09/2018	06/03/2019
ET/EA/001/15	Sibata LD-3B	597227	19/07/2018	18/01/2019
			17/01/2019	16/07/2019

Certificate of Calibration

Calibration Certification Information

Cal. Date: March 21, 2018

Rootsmeter S/N: 438320

Ta: 293

°K
Operator: Jim Tisch

Pa: 756.9

mm Hg
Calibration Model #: TE-5025A

Calibrator S/N: 3480

Run	Vol. Init (m3)	Vol. Final (m3)	ΔVol. (m3)	ΔTime (min)	ΔP (mm Hg)	ΔH (in H2O)
1	1	2	1	1.4200	3.2	2.00
2	3	4	1	1.0000	6.4	4.00
3	5	6	1	0.8950	7.9	5.00
4	7	8	1	0.8570	8.8	5.50
5	9	10	1	0.7070	12.7	8.00

Data Tabulation

Vstd (m3)	Qstd (x-axis)	$\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)}$ (y-axis)	Va	Qa (x-axis)	$\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)}$ (y-axis)
1.0087	0.7103	1.4233	0.9958	0.7012	0.8799
1.0044	1.0044	2.0129	0.9915	0.9915	1.2443
1.0024	1.1200	2.2505	0.9896	1.1057	1.3912
1.0012	1.1682	2.3603	0.9884	1.1533	1.4591
0.9959	1.4087	2.8467	0.9832	1.3907	1.7598
QSTD	m=	2.04113	QA	m=	1.27812
	b=	-0.03040		b=	-0.01879
	r=	0.99994		r=	0.99994

Calculations


Vstd=	$\Delta Vol((Pa-\Delta P)/Pstd)(Tstd/Ta)$	Va=	$\Delta Vol((Pa-\Delta P)/Pa)$
Qstd=	$Vstd/\Delta Time$	Qa=	$Va/\Delta Time$
For subsequent flow rate calculations:			
Qstd=	$1/m \left(\left(\sqrt{\Delta H \left(\frac{Pa}{Pstd} \right) \left(\frac{Tstd}{Ta} \right)} \right) - b \right)$	Qa=	$1/m \left(\left(\sqrt{\Delta H \left(\frac{Ta}{Pa} \right)} \right) - b \right)$

Standard Conditions

Tstd:	298.15 °K
Pstd:	760 mm Hg
Key	
ΔH: calibrator manometer reading (in H2O)	
ΔP: rootsmeter manometer reading (mm Hg)	
Ta: actual absolute temperature (°K)	
Pa: actual barometric pressure (mm Hg)	
b: intercept	
m: slope	

RECALIBRATION

US EPA recommends annual recalibration per 1998 40 Code of Federal Regulations Part 50 to 51, Appendix B to Part 50, Reference Method for the Determination of Suspended Particulate Matter in the Atmosphere, 9.2.17, page 30



Calibration Report
of
High Volume Air Sampler


Manufacturer : Graseby (Model No. GS2310) **Date of Calibration** : 19 December 2018

Serial No. : 1934 (ET / EA / 003 / 25) **Calibration Due Date** : 18 February 2019

Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results :	Flow recorder reading (cfm)	58	52	46	39	28
	Qstd (Actual flow rate, m ³ /min)	1.81	1.61	1.38	1.13	0.89
	Pressure : 765.06 mm Hg	Temp. : 292 K				

Sampler 1934 Calibration Curve
Site: San Wai (ASR1a)

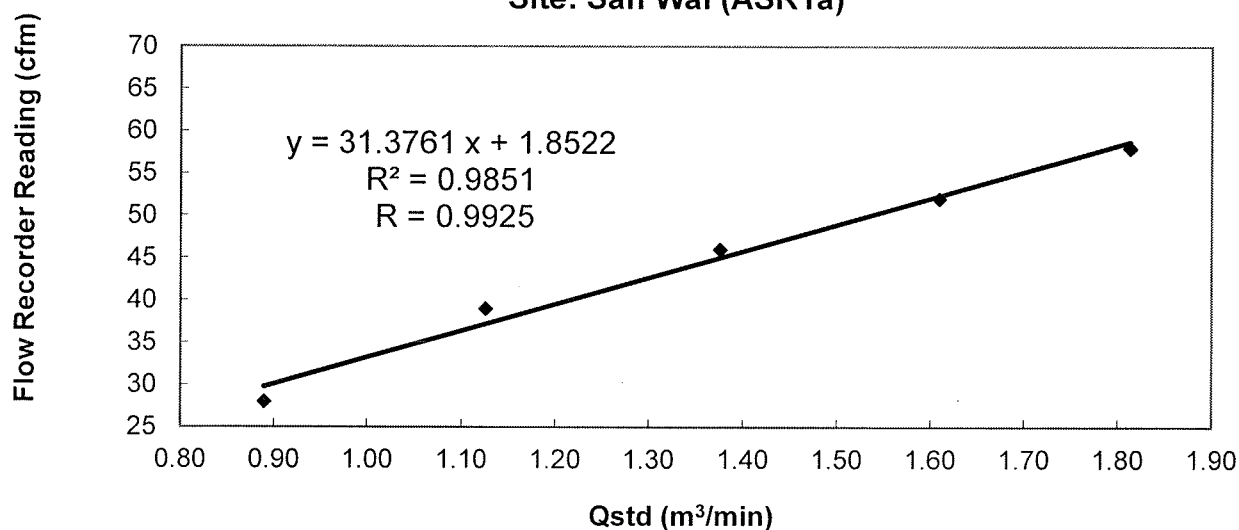

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.


The high volume sampler complies* / does not comply* with the specified requirements and is deemed acceptable* / unacceptable* for use.

Calibrated by :

LIAO, Yun Chao
(Technician)

Approved by :

LAU, Chi Leung
(Environmental Team Leader)



Calibration Report
of
High Volume Air Sampler


Manufacturer : Graseby (Model No. GS2310) **Date of Calibration** : 19 December 2018

Serial No. : 9998 (ET / EA / 003 / 12) **Calibration Due Date** : 18 February 2019

Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results :	Flow recorder reading (cfm)	50	47	40	35	26
	Qstd (Actual flow rate, m ³ /min)	1.79	1.68	1.47	1.20	0.91
	Pressure : 769.56 mm Hg	Temp. : 292 K				

Sampler 9998 Calibration Curve
Site: San Wai (ASR2a)

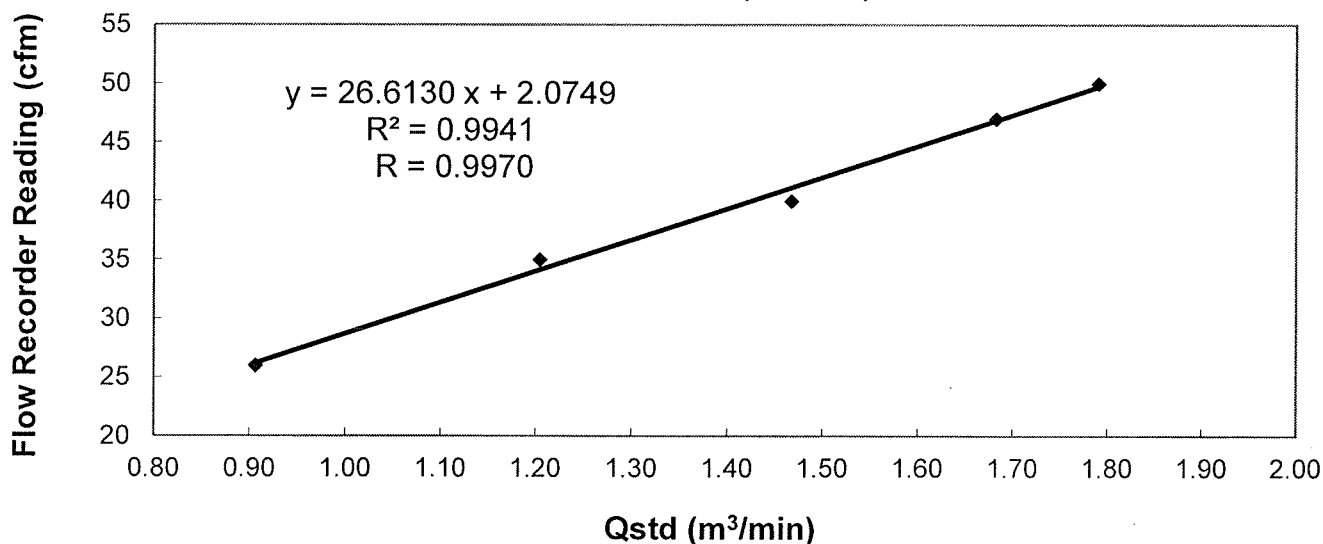

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.


The high volume sampler complies* / ~~does not comply*~~ with the specified requirements and is deemed acceptable* / unacceptable* for use.

Calibrated by :

LIAO, Yun Chao
(Technician)

Checked by :

LAU, Chi Leung
(Environmental Team Leader)



Internal Calibration Report


of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 18 October 2018

Serial No. : 8X4282 (ET/EA/001/05) **Calibration Due Date** : 17 April 2019

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition

Results	Dust Monitor (CPM)	38	67	104
	High Volume Air Sampler (ug/m ³)	88	175	244
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 1 December 2018	

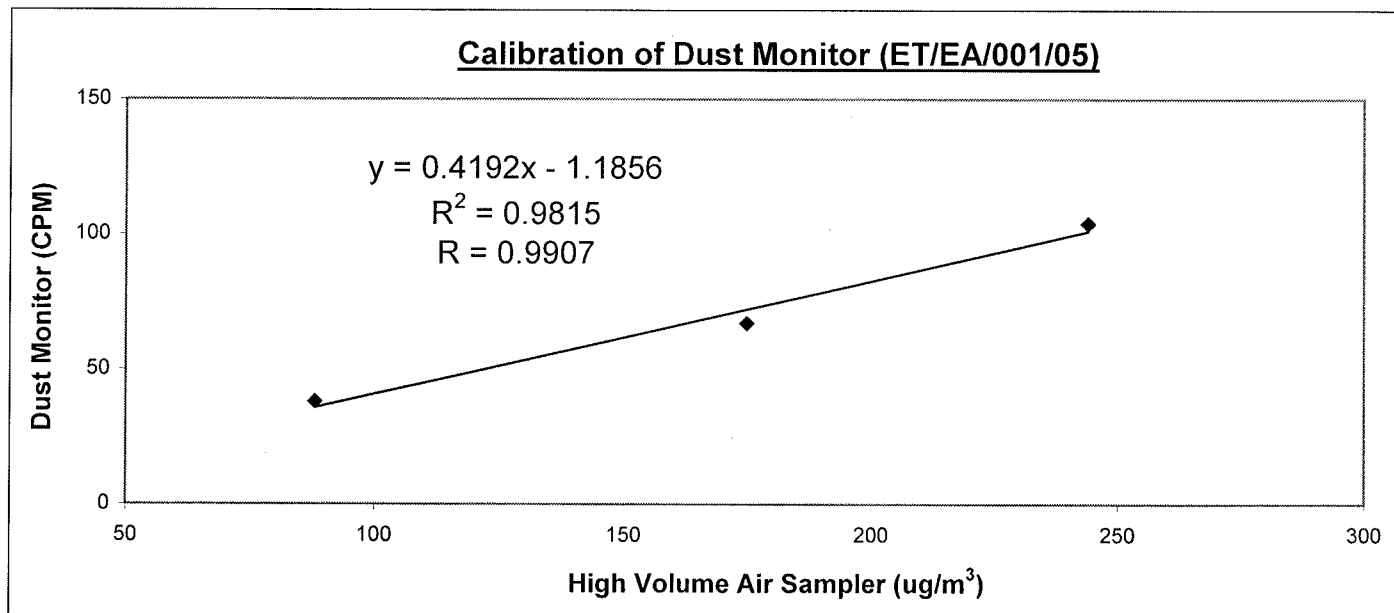


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / ~~unacceptable~~ * for use.


Calibrated by :


LI, Lok Yin
(Technician)

Checked by :


LAU, Chi Leung
(Environmental Team Leader)

- END OF REPORT -




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration :** 15 October 2018

Serial No. : 014746 (ET/EA/001/06) **Calibration Due Date :** 14 April 2019

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition


Results :	Dust Monitor (CPM)	25	70	165
	High Volume Air Sampler (ug/m ³)	53	106	277
	High Volume Air Sampler Serial No.: 1177 Calibration Due Date: 1 December 2018			

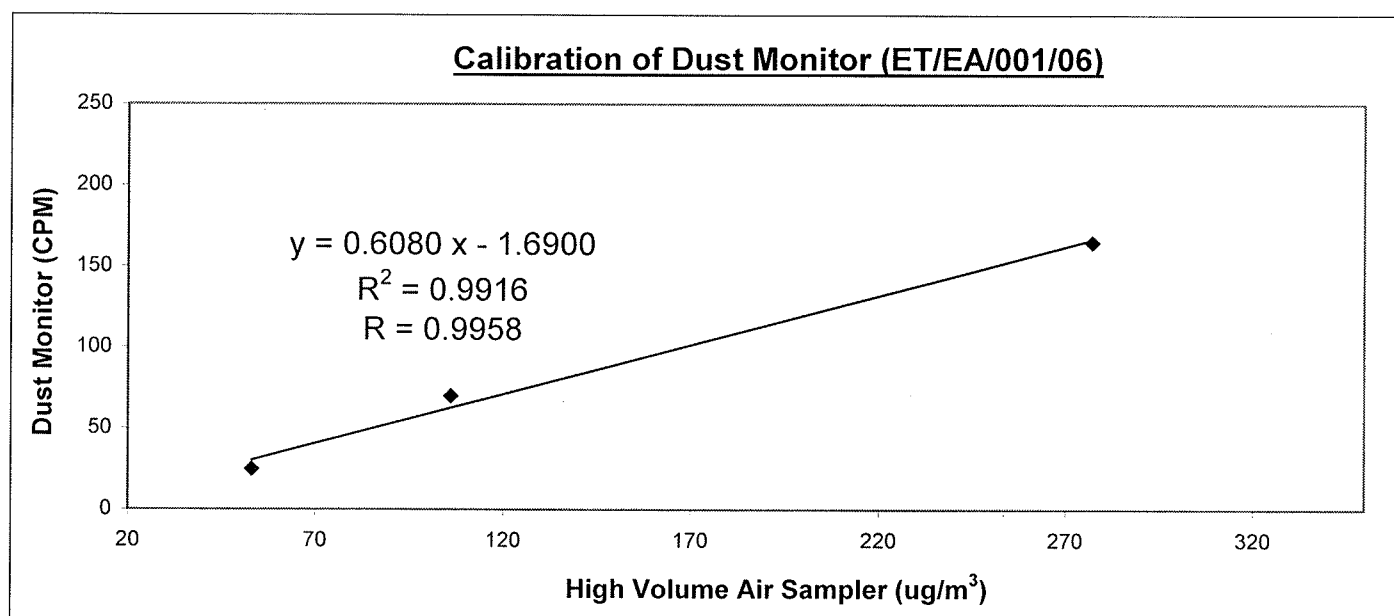


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after three-point calibration.

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / ~~unacceptable~~ * for use.


Calibrated by :


LI, Lok Yin
(Technician)

Checked by :


LAU, Chi Leung
(Environmental Team Leader)

- END OF REPORT -



Internal Calibration Report


of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 22 September 2018

Serial No. : 135261 (ET/EA/001/08) **Calibration Due Date** : 21 March 2019

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition


Results :	Dust Monitor (CPM)	37	75	186
	High Volume Air Sampler (ug/m ³)	50	125	272
	High Volume Air Sampler Serial No.:1177		Calibration Due Date: 2 October 2018	

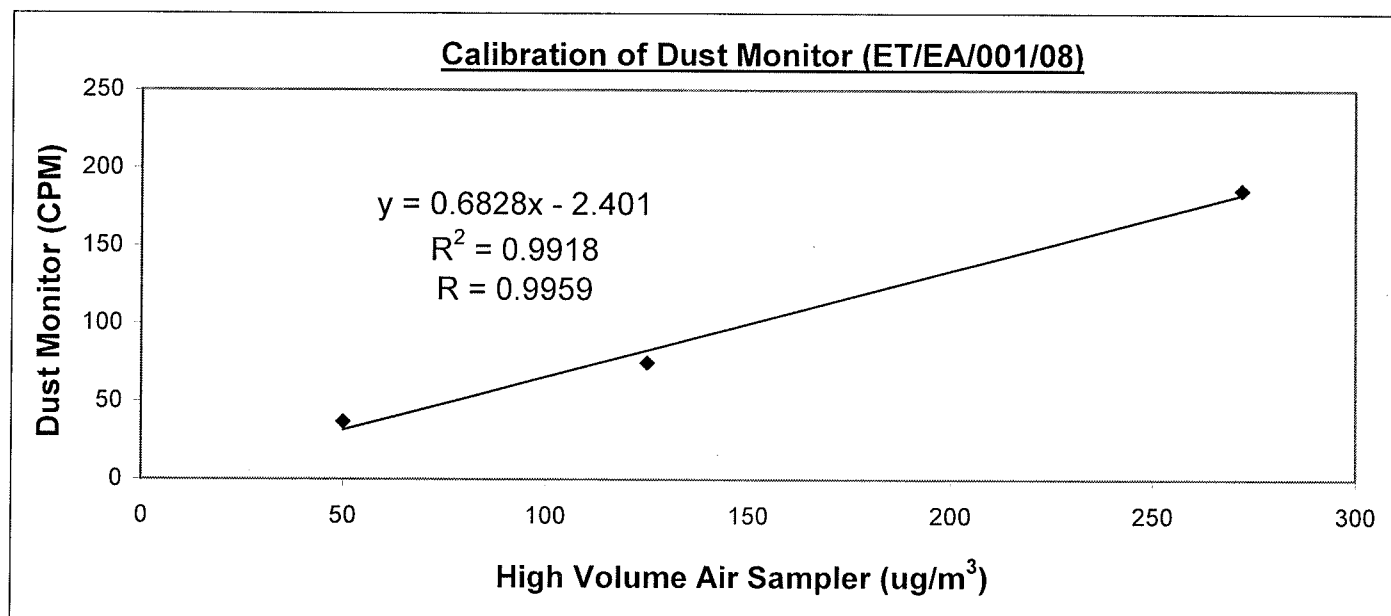


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.


Calibrated by :


Li Lok Yin
(Technician)

Checked by :


LAU, Chi Leung
(Environmental Team Leader)

- END OF REPORT -




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 15 October 2018

Serial No. : 1Z5635 (ET/EA/001/10) **Calibration Due Date** : 14 April 2019


Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition


Results :	Dust Monitor (CPM)	47	85	207
	High Volume Air Sampler ($\mu\text{g}/\text{m}^3$)	65	146	307
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 1 December 2018	

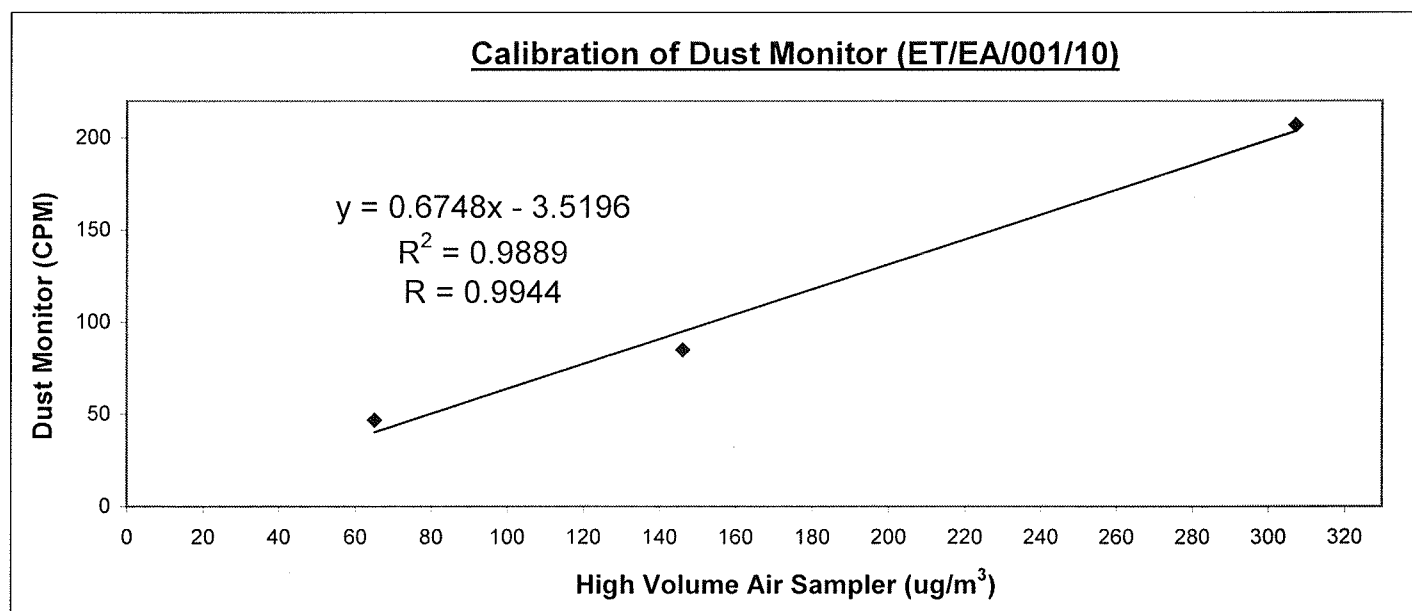


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : 
LI, Lok Yin
(Technician)

Checked by : 
LAU, Chi Leung
(Environmental Team Leader)

- END OF REPORT -




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration :** 16 November 2018

Serial No. : 255863 (ET/EA/001/11) **Calibration Due Date :** 15 May 2019


Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition

Results	Dust Monitor (CPM)	33	62	166
	High Volume Air Sampler (ug/m ³)	44	105	256
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 1 December 2018	

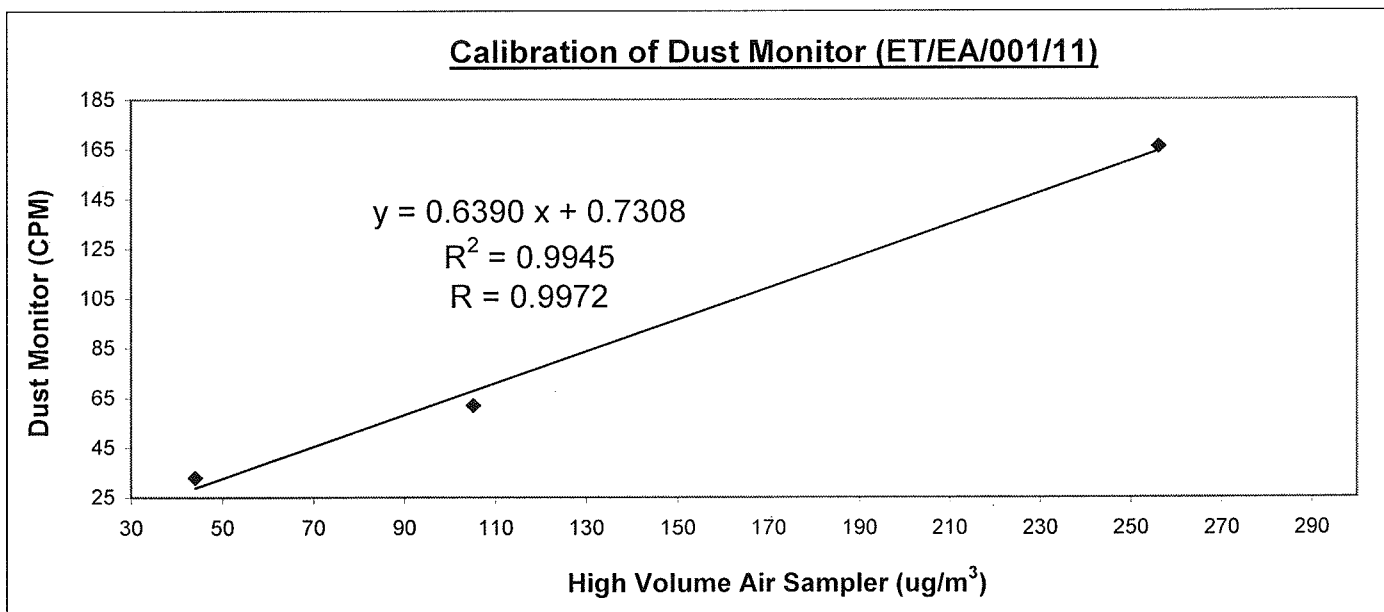

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / ~~unacceptable~~ * for use.

Calibrated by : 
LI, Lok Yin
(Technician)

Checked by : 
LAU, Chi Leung
(Environmental Team Leader)




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-5) Date of Calibration : 20 December 2018

Serial No. : 4Y1613 (ET/EA/001/13) Calibration Due Date : 19 June 2019


Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition


Results	Dust Monitor (CPM)	33	86	196
	High Volume Air Sampler ($\mu\text{g}/\text{m}^3$)	47	144	306
	High Volume Air Sampler Serial No.: 1177 Calibration Due Date: 29 January 2019			

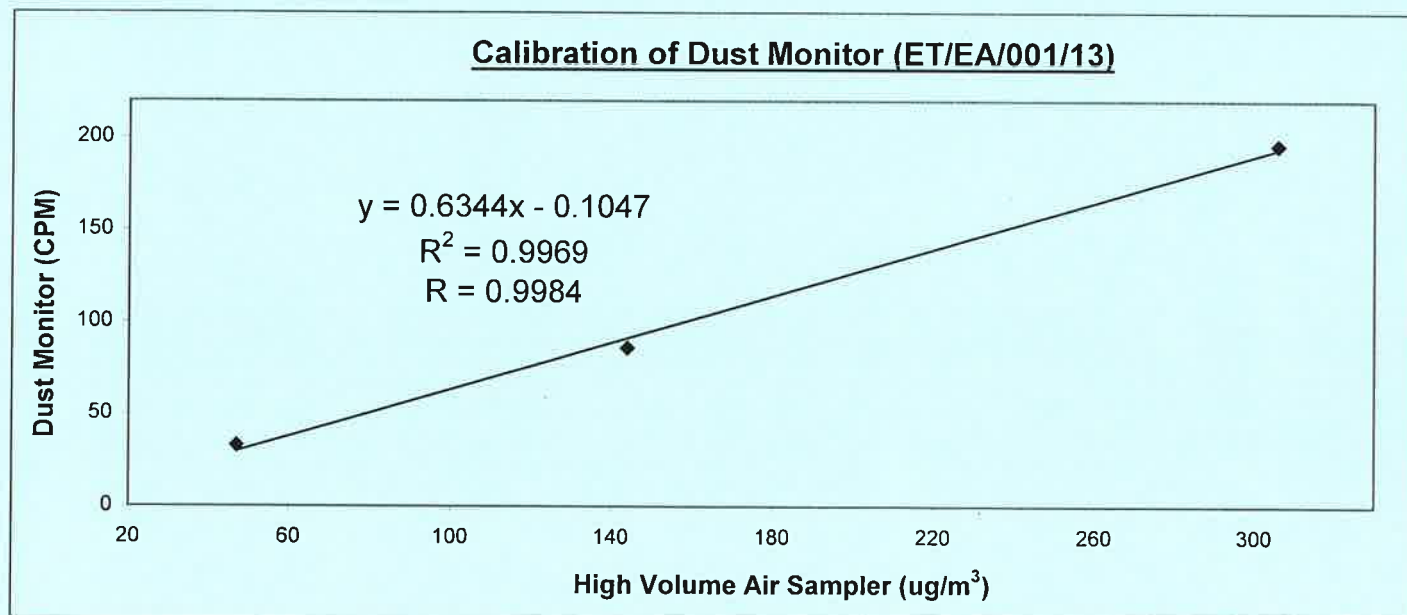


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : 
LI, Lok Yin
(Technician)

Checked by : 
LAU, Chi Leung
(Environmental Team Leader)

- END OF REPORT -




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration :** 07 September 2018

Serial No. : 597340 (ET/EA/001/14) **Calibration Due Date :** 06 March 2019

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition

Results :	Dust Monitor (CPM)	28	54	176
	High Volume Air Sampler (ug/m ³)	37	102	275
	High Volume Air Sampler Serial No.: 1177 Calibration Due Date: 2 October 2018			

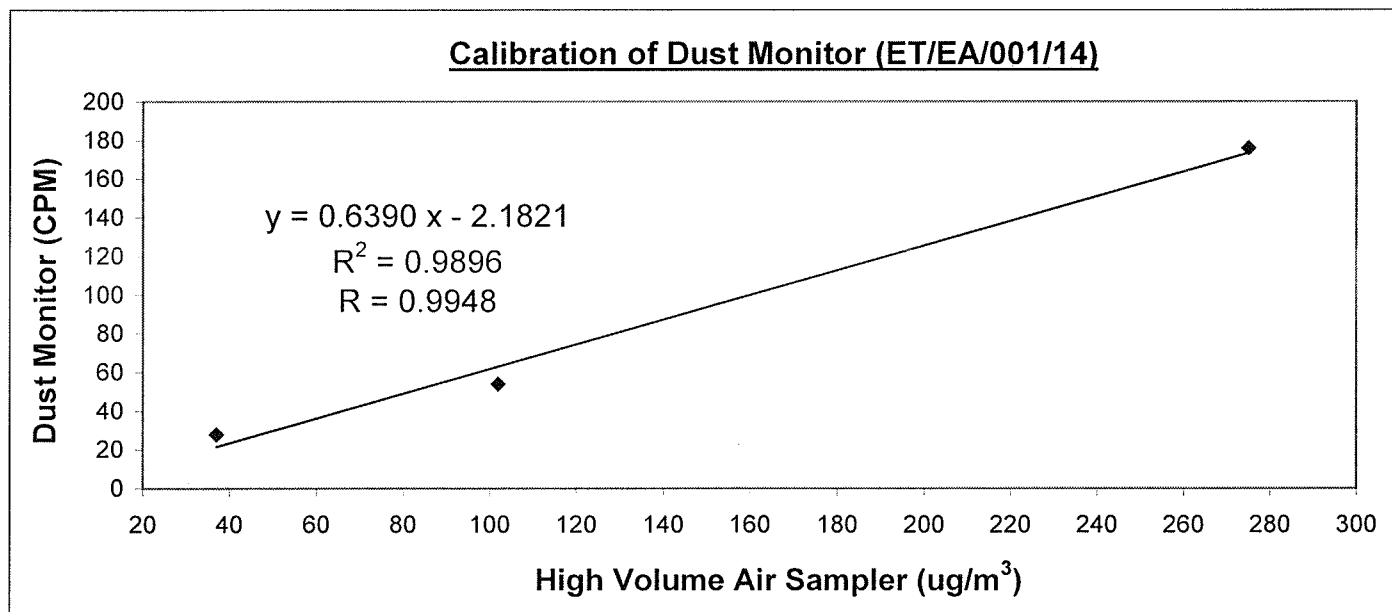


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : LI, Lok Yin
(Technician)

Checked by : LAU, Chi Leung
(Environmental Team Leader)




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 19 July 2018

Serial No. : 597227 (ET/EA/001/15) **Calibration Due Date** : 18 Jan 2019

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition

Results	Dust Monitor (CPM)	26	68	176
	High Volume Air Sampler (ug/m ³)	32	113	259
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 3 August 2018	

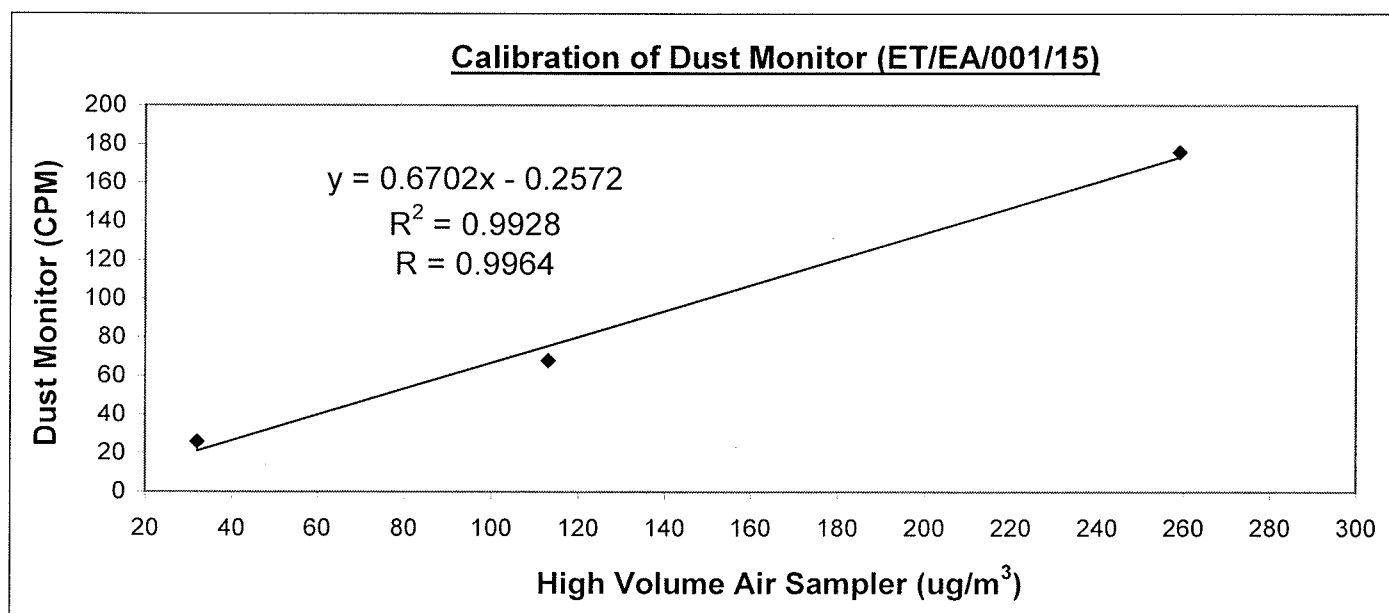


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / ~~unacceptable~~ * for use.

Calibrated by : CHUNG, Ka Ho
(Technician)

Checked by : LAU, Chi Leung
(Environmental Team Leader)




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) Date of Calibration : 17 Jan 2019

Serial No. : 597227 (ET/EA/001/15) Calibration Due Date : 16 July 2019


Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Samper together under the same environmental condition


Results	Dust Monitor (CPM)	28	66	172
	TSP (ug/m ³)	34	112	263
	High Volume Air Sampler Serial No.: 1177 Calibration Due Date: 29 January 2019			

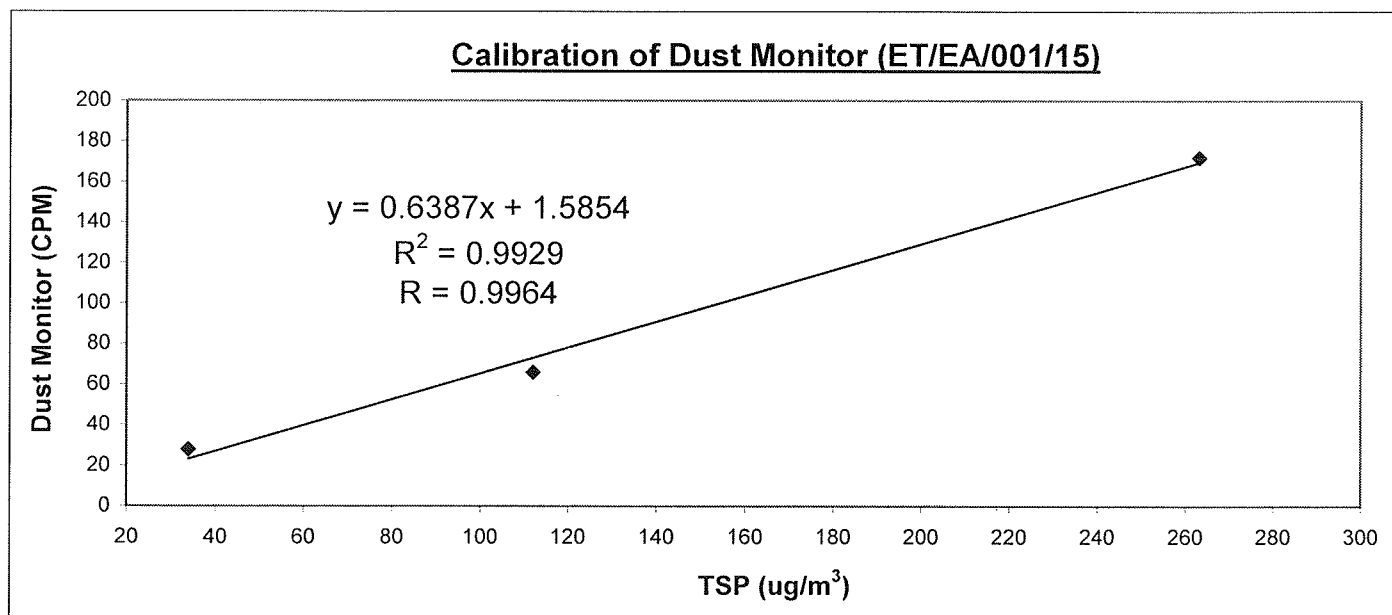

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : 
LI, Lok Yin
(Technician)

Checked by : 
LAU, Chi Leung
(Environmental Team Leader)

Appendix D2

Impact Air Quality Monitoring Results

Summary of Impact 1-hour TSP Monitoring Results

Air Quality Monitoring Station : ASR1a

Date	Weather	Temperature (°C)	Monitoring Period		1-hr TSP ($\mu\text{g}/\text{m}^3$)
			Start	Finish	
04/01/2019	Fine	18	08:47	09:47	65
04/01/2019	Fine	18	09:47	10:47	60
04/01/2019	Fine	18	10:47	11:47	62
10/01/2019	Fine	16	08:58	09:58	66
10/01/2019	Fine	16	09:58	10:58	72
10/01/2019	Fine	16	10:58	11:58	72
16/01/2019	Cloudy	18	09:00	10:00	60
16/01/2019	Cloudy	18	10:00	11:00	55
16/01/2019	Cloudy	18	11:00	12:00	55
22/01/2019	Fine	19	08:51	09:51	68
22/01/2019	Fine	19	09:51	10:51	72
22/01/2019	Fine	19	10:51	11:51	68
28/01/2019	Cloudy	20	14:58	15:58	47
28/01/2019	Cloudy	20	15:58	16:58	48
28/01/2019	Cloudy	19	16:58	17:58	47
Min					47
Max					72
Average					61

Air Quality Monitoring Station : ASR2b

Date	Weather	Temperature (°C)	Monitoring Period		1-hr TSP ($\mu\text{g}/\text{m}^3$)
			Start	Finish	
04/01/2019	Fine	18	08:56	09:56	55
04/01/2019	Fine	18	09:56	10:56	59
04/01/2019	Fine	18	10:56	11:56	59
10/01/2019	Fine	16	13:14	14:14	79
10/01/2019	Fine	16	14:14	15:14	74
10/01/2019	Fine	16	15:14	16:14	72
16/01/2019	Cloudy	18	13:17	14:17	67
16/01/2019	Cloudy	18	14:17	15:17	65
16/01/2019	Cloudy	18	15:17	16:17	67
22/01/2019	Fine	19	09:00	10:00	89
22/01/2019	Fine	19	10:00	11:00	93
22/01/2019	Fine	19	11:00	12:00	93
28/01/2019	Cloudy	20	15:00	16:00	63
28/01/2019	Cloudy	20	16:00	17:00	58
28/01/2019	Cloudy	19	17:00	18:00	65
Min					55
Max					93
Average					71

Summary of Impact 24-hour TSP Monitoring Results

Air Quality Monitoring Station : ASR1a



Start		Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Paper Weight (g)		Conc. (µg/m ³)	Weather Condition
Date	Time	Date	Time	Initial	Final		Initial	Final		Initial	Final		
04/01/2019	08:50	05/01/2019	08:50	25325.64	25349.64	24	1.0246	1.0246	1.0246	2.6489	2.7448	65	Fine
10/01/2019	09:05	11/01/2019	09:05	25349.64	25373.64	24	1.0246	1.0246	1.0246	2.6464	2.7511	71	Fine
16/01/2019	09:05	17/01/2019	09:05	25373.64	25397.64	24	1.0246	1.0246	1.0246	2.6772	2.7863	74	Cloudy
22/01/2019	09:00	23/01/2019	09:00	25397.64	25421.64	24	0.9609	0.9609	0.9609	2.6053	2.6924	63	Fine
28/01/2019	15:50	29/01/2019	15:50	25421.64	25445.64	24	0.9609	0.9609	0.9609	2.6708	2.7773	77	Cloudy
											Min	63	
											Max	77	
											Average	70	

Air Quality Monitoring Station : ASR2b


Start		Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Paper Weight (g)		Conc. (µg/m ³)	Weather Condition
Date	Time	Date	Time	Initial	Final		Initial	Final		Initial	Final		
04/01/2019	09:00	05/01/2019	09:00	22070.45	22094.45	24	1.1245	1.1245	1.1245	2.6371	2.7472	68	Fine
10/01/2019	13:20	11/01/2019	13:20	22094.45	22118.45	24	1.1245	1.1245	1.1245	2.6256	2.7340	67	Fine
16/01/2019	13:20	17/01/2019	13:20	22118.45	22142.45	24	1.1245	1.1245	1.1245	2.6345	2.7478	70	Cloudy
22/01/2019	09:05	23/01/2019	09:05	22142.45	22166.45	24	1.1245	1.1245	1.1245	2.6687	2.7788	68	Fine
28/01/2019	15:10	29/01/2019	15:10	22166.45	22190.45	24	1.1245	1.1245	1.1245	2.6233	2.7431	74	Cloudy
											Min	67	
											Max	74	
											Average	69	

Appendix D3


Graphical Plots of Impact Air Quality Monitoring Results

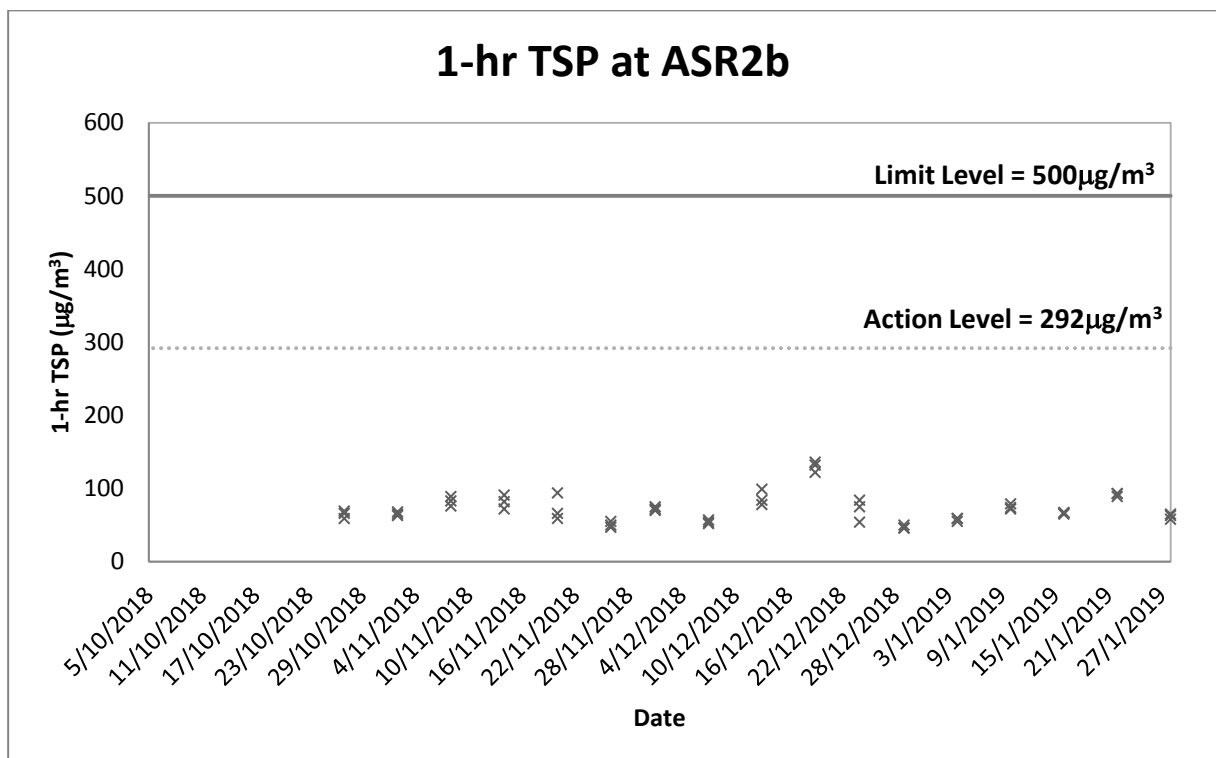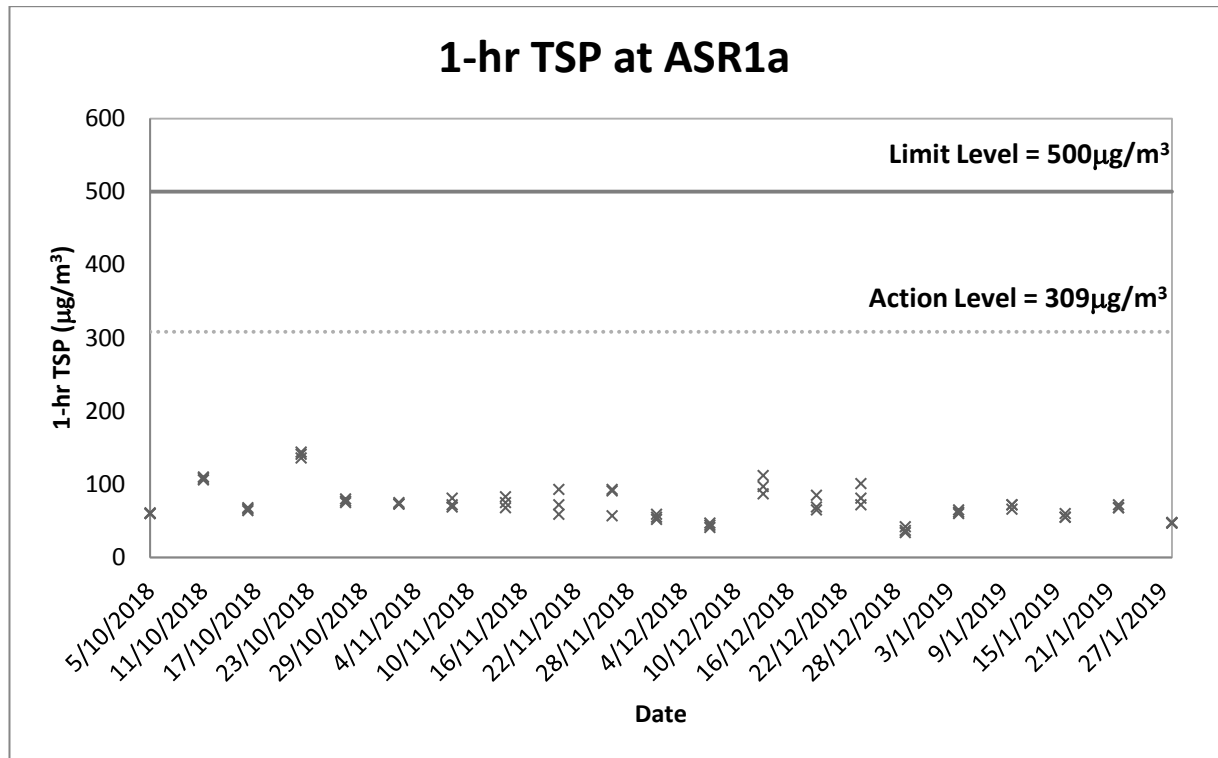

24-hr TSP at ASR1a

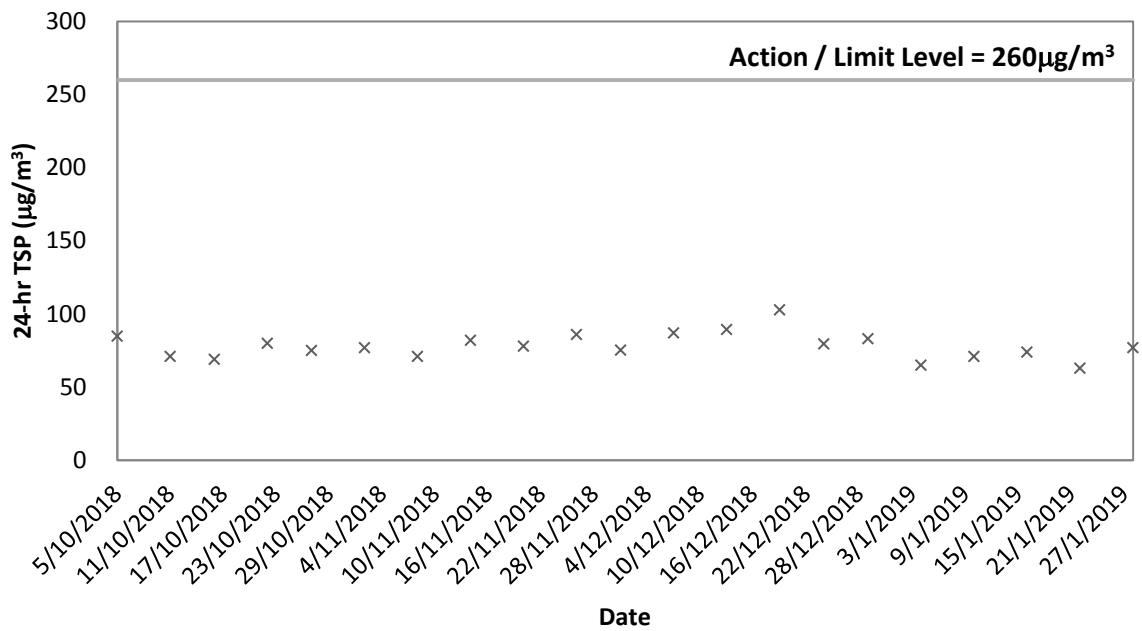

24-hr TSP at ASR2b

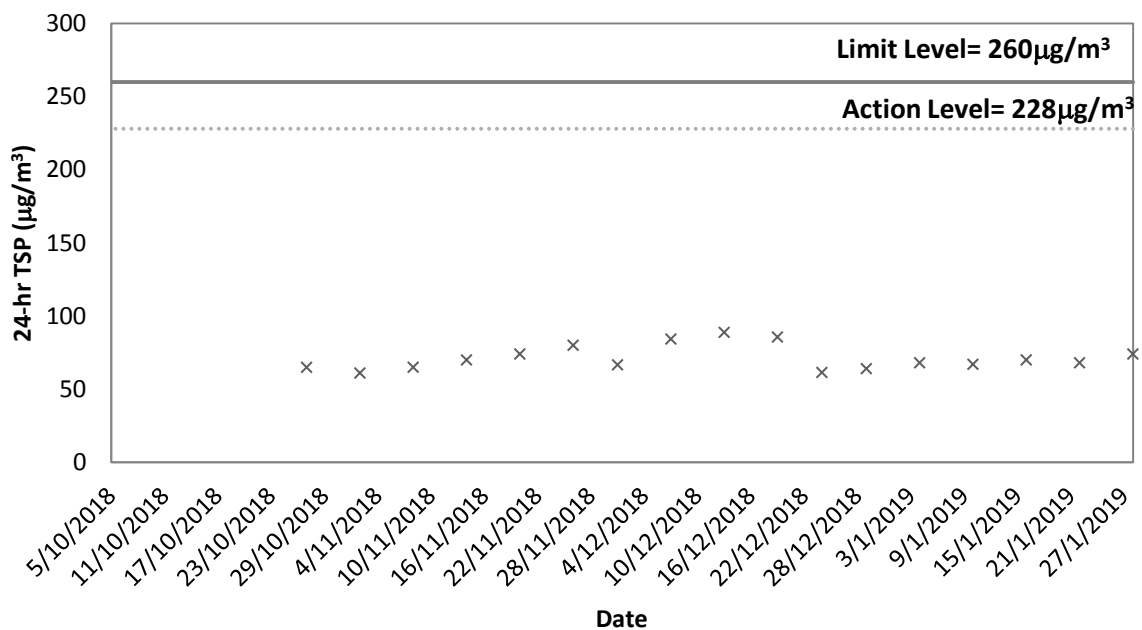

Appendix E1

Calibration Certificates for Impact Noise Monitoring Equipment

**Summary of Calibration Certificates for Noise Monitoring Equipment
used in this reporting month**

Equipment	Equip No.	Serial No.	Calib. Date	Due Date
Sound Level Calibrator (Castle GA607)	ET/EN/002/07	038641	20/03/2018	19/03/2019
Sound Level Meter (Rion NL-52)	ET/EN/003/17	00264519	06/03/2018	06/03/2019



Calibration Certificate

Certificate No. **801750**

Page **1** of **2** Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q80695

Date of receipt : 13-Feb-18

Item Tested

Description : Thermo-Anemometer

Manufacturer : AZ Instrument

Model : AZ 8908

I.D. : ET/EN/001/05

Serial No. : 1064869

Test Conditions

Date of Test : 7-Mar-18

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Supply Voltage : --

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Calibration procedure : T03, Z04.

Test Results

A correction factor of $\times 1.1$ is required to bring the meter reading to within the manufacturer's specification.
The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S155	Std. Anemometer	711600	NIM-PRC
S223C	Std. Thermometer	705236	NIM-PRC

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by : 

W M Ng

Approved by : 

Steve Kwan

Date: 7-Mar-18

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646



Calibration Certificate

Certificate No. 801750

Page 2 of 2 Pages

Results :

1. Velocity

Applied Value (m/s)	UUT Reading (m/s)	Corrected Reading (UUT Rdg. \times 1.1)	Mfr's Spec.
0.00	0.0	0.0	\pm (3% of reading + 0.2 m/s)
2.50	2.3	2.5	
5.00	4.7	5.2	
10.00	*9.1	10.0	
15.00	*13.7	15.1	
19.00	*17.3	19.0	

2. Temperature

Applied Value (°C)	UUT Reading (°C)	Mfr's Spec.
22.50	22.2	\pm 1 °C

Remark : 1. UUT : Unit-Under-Test

2. Uncertainty : \pm (0.9% + 0.16 m/s) for Velocity, \pm 0.1 °C for Temperature, for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1 022 hPa

4. *Out of Specification

----- END -----



Hong Kong Calibration Ltd.

香港校正有限公司

Calibration Certificate

Certificate No. 802480

Page 1 of 2 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q80960

Date of receipt : 12-Mar-18

Item Tested

Description : Acoustic Calibrator

Manufacturer : Castle

Model : GA607

I.D. : ET/EN/002/07

Serial No. : 038641

Test Conditions

Date of Test : 20-Mar-18

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Supply Voltage : --

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure : IEC 60942, F06, F20, Z02.

Test Results

All results were within the IEC 60942 Class 1 specification.

The results are shown in the attached page(s).

Main Test equipment used:

Equipment No.	Description	Cert. No.	Traceable to
S014	Spectrum Analyzer	707126	NIM-PRC & SCL-HKSAR
S240	Sound Level Calibrator	703741	NIM-PRC & SCL-HKSAR
S041	Universal Counter	802061	SCL-HKSAR
S206	Sound Level Meter	707129	SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by :

Elva Chong

Approved by :

Kin Wong

Date: 20-Mar-18

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full.

E



Calibration Certificate

Certificate No. 802480

Page 2 of 2 Pages

Results :

1. Generated Sound Pressure Level

UUT Nominal Value (dB)	Measured Value (dB)	IEC 60942 Class 1 Spec.
94.0	94.1	± 0.4 dB

Uncertainty : ± 0.2 dB

2. Short-term Level Fluctuation : 0.0 dB

IEC 60942 Class 1 Spec. : ± 0.1 dB

Uncertainty : ± 0.01 dB

3. Frequency

UUT Nominal Value (kHz)	Measured Value (kHz)	IEC 60942 Class 1 Spec.
1	1.000	± 1 %

Uncertainty : $\pm 3.6 \times 10^{-6}$

4. Total Distortion : < 2.8 %

IEC 60942 Class 1 Spec. : < 4 %

Uncertainty : ± 2.3 % of reading

Remark : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1 018 hPa.

----- END -----



Calibration Certificate

Certificate No. **801836**

Page 1 of 3 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q80729

Date of receipt : 23-Feb-18

Item Tested

Description : Sound Level Meter

Manufacturer : Rion

I.D. : --

Model : NL-52

Serial No. : 00264519

Test Conditions

Date of Test : 6-Mar-18

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure: Z01, IEC 61672.

Test Results

All results were within the IEC 61672 Type 1 or manufacturer's specification.

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S017	Multi-Function Generator	C170120	SCL-HKSAR
S240	Sound Level Calibrator	703741	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by :

Elva Chong

Approved by :

Kin Wong

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

Date: 6-Mar-18



Calibration Certificate

Certificate No. 801836

Page 2 of 3 Pages

Results :

1. Self-generated noise: 14.6 dBA (Mfr's Spec ≤ 17 dBA)

2. Acoustical signal test

UUT Setting				Applied Value (dB)	UUT Reading (dB)
Range (dB)	Frequency Weighting	Time Weighting	Octave Filter		
20 ~ 130	A	F	OFF	94.0	94.0
		S	OFF		94.0
	C	F	OFF		94.0
	Z	F	OFF		94.1
	A	F	OFF	114.0	114.1
		S	OFF		114.1
	C	F	OFF		114.1
	Z	F	OFF		114.1

IEC 61672 Type 1 Spec. : ± 1.1 dB

Uncertainty : ± 0.1 dB

3 Electrical signal tests of frequency weightings (A weighting)

Frequency	Attenuation (dB)	IEC 61672 Type 1 Spec.
31.5 Hz	-39.8	- 39.4 dB, ± 2 dB
63 Hz	-26.3	- 26.2 dB, ± 1.5 dB
125 Hz	-16.2	- 16.1 dB, ± 1.5 dB
250 Hz	-8.7	- 8.6 dB, ± 1 dB
500 Hz	-3.3	- 3.2 dB, ± 1.4 dB
1 kHz	0.0 (Ref)	0 dB, ± 1.1 dB
2 kHz	+1.2	+ 1.2 dB, ± 1.6 dB
4 kHz	+0.9	+ 1.0 dB, ± 1.6 dB
8 kHz	-1.1	- 1.1 dB, + 2.1 dB ~ -3.1 dB
16 kHz	-7.1	- 6.6 dB, + 3.5 dB ~ - 17.0 dB

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 801836

Page 3 of 3 Pages

4. Frequency & Time weightings at 1 kHz

4.1 Frequency Weighting (Fast)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
A	94.0	94.0 (Ref.)	- -	± 0.4 dB
C	94.0	94.0	0.0	
Z	94.0	94.0	0.0	

4.2 Time Weighting (A-weighted)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
Fast	94.0	94.0 (Ref.)	- -	± 0.3 dB
Slow	94.0	94.0	0.0	
Time-averaging	94.0	94.0	0.0	

Uncertainty : ± 0.1 dB

Remarks : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1 027 hPa.

4. Preamplifier model : NH-25 , S/N : 64644

5. Firmware Version: 1.7

6. Power Supply Check: OK

7. The UUT was adjusted with the laboratory's sound calibrator at the reference sound pressure level before the calibration.

----- END -----

Appendix E2

Impact Noise Monitoring Results

Day-time Noise Monitoring

Monitoring Station: NSR1a

Date	Weather	Temperature (°C)	Start Time (hh:mm)	End Time (hh:mm)	Noise Level at NSR1a, dB (A)			Wind Speed (m/s)
					Leq (30min)	L10 (30min)	L90 (30min)	
04/01/19	Fine	18	08:47	09:17	68.1	72.4	66.5	0.3
10/01/19	Fine	16	09:10	09:40	65.4	68.7	63.1	0.4
16/01/19	Cloudy	18	08:55	09:25	67.4	70.9	66.0	0.3
22/01/19	Fine	19	09:05	09:35	67.2	69.7	66.4	0.3
28/01/19	Cloudy	21	15:45	16:15	62.1	64.8	58.2	0.1
Min					62.1	64.8	58.2	
Max					68.1	72.4	66.5	
Logarithmic Average for normal weekdays					66.5	70.0	64.9	

Monitoring Station: NSR2b


Date	Weather	Temperature (°C)	Start Time (hh:mm)	End Time (hh:mm)	Noise Level at NSR2b, dB (A)			Wind Speed (m/s)
					Leq (30min)	L10 (30min)	L90 (30min)	
04/01/19	Fine	18	09:30	10:00	69.2	73.9	67.0	0.4
10/01/19	Fine	16	13:21	13:51	67.2	70.6	66.0	0.4
16/01/19	Cloudy	18	13:20	13:50	68.5	73.2	65.1	0.5
22/01/19	Fine	19	10:11	10:41	68.1	72.7	67.0	0.4
28/01/19	Cloudy	21	15:05	15:35	68.3	69.1	65.8	0.1
Min					67.2	69.1	65.1	
Max					69.2	73.9	67.0	
Logarithmic Average for normal weekdays					68.3	72.2	66.2	

(*) : 3dB(A) correction was added to the results during the free-field noise measurements


Appendix E3

Graphical Plots of Impact Noise Monitoring Data

Noise Level at NSR1a

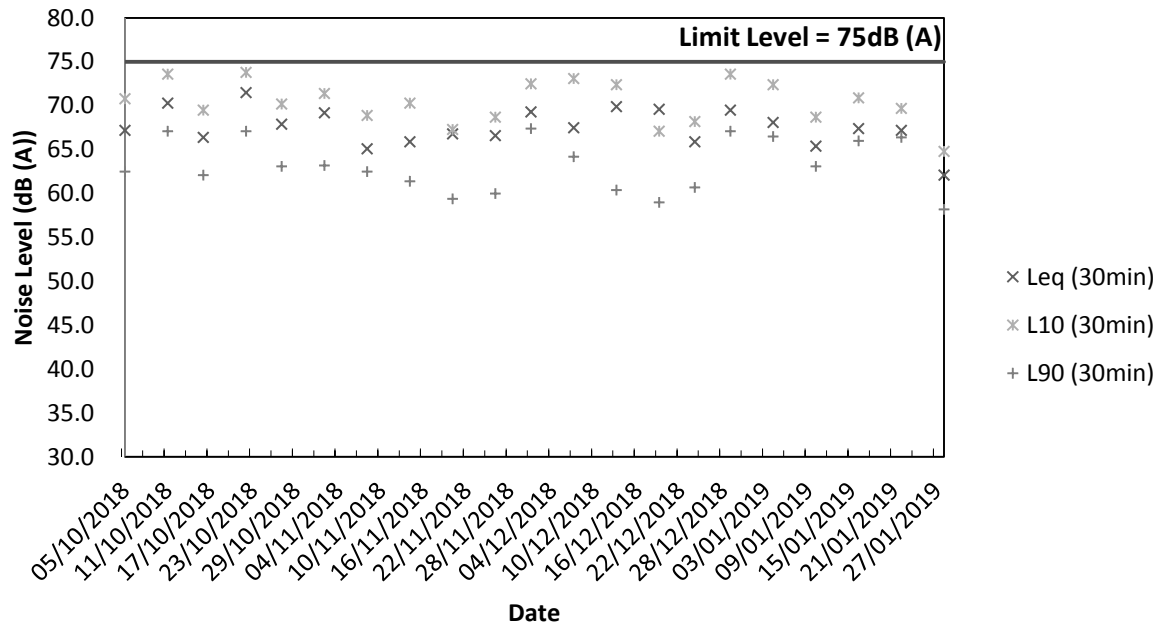

Noise Level at NSR2b

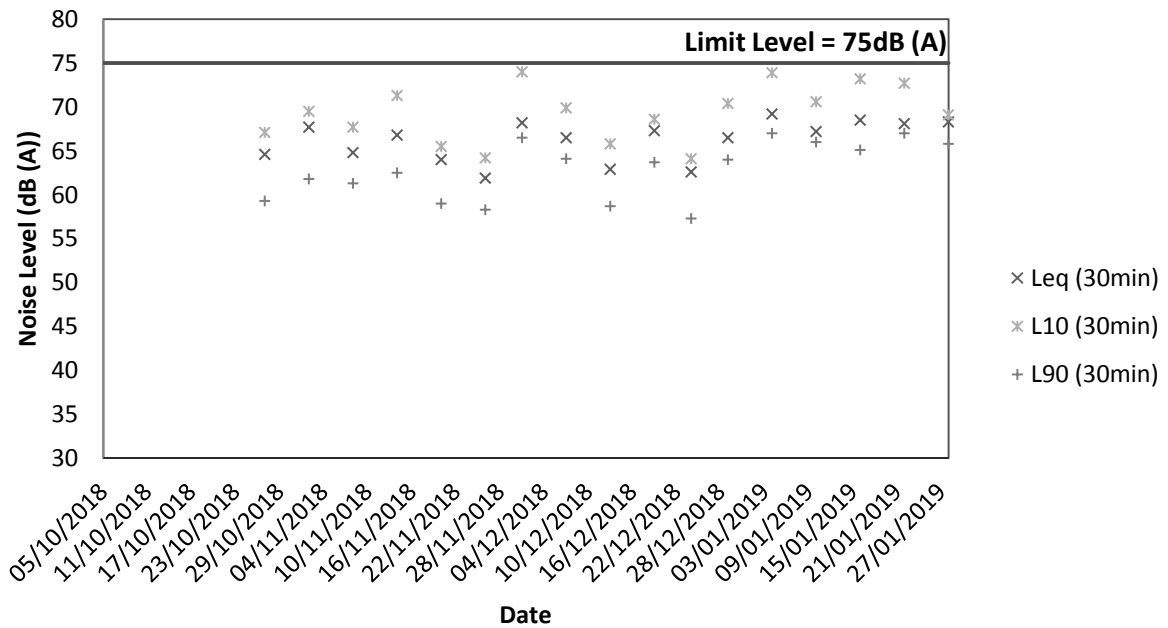

Appendix F1

Calibration Certificates for Impact Water Quality Monitoring Equipments



Performance Check of Turbidity Meter

Equipment Ref. No. : ET/0505/011 Manufacturer : HACH
Model No. : 2100Q Serial No. : 1260C018574
Date of Calibration : 16/11/2018 Due Date : 15/2/2019

Theoretical Value of Turbidity Standard (NTU)	Measured Value (NTU)	Difference % *
20	20.4	2.0%
100	99.7	-0.3%
800	786	-1.8%


(*) Difference = (Measured Value – Theoretical Value) / Theoretical Value x 100

Acceptance Criteria

Difference : -5 % to 5 %

The turbidity meter complies * / ~~does not comply~~ * with the specified requirements and is deemed acceptable * / ~~unacceptable~~ * for use. Measurements are traceable to national standards.

Prepared by : 

Checked by : 



Calibration Report of Dissolved Oxygen Meter (*In situ* Measurement)

Equipment Ref. No. : ET/EW/008/009 Manufacturer : YSI
Model No. : Pro 2030 Serial No. : 16LL100372
Calibration Date : 2/12/2018 Calibration Due Date : 1/3/2019

Temperature Verification by Reference Thermometer (ET/0521/028)

	Temperature Reading (°C)	Correction (°C)	Corrected Temperature (°C)	Difference (°C)
Reference Thermometer	20.2	0.0	20.2	0.0
DO Meter	20.2	0.0	20.2	

Criteria: Difference between corrected temperature from DO meter and reference thermometer : $< \pm 0.5^{\circ}\text{C}$

Zero Point Checking

DO meter reading (mg/L)	0.02
-------------------------	------

Criteria: Zero checking: 0.0 mg/L

Linearity Checking of Dissolved Oxygen Content by APHA 19ed 4500-O G

Purging time, min	Expected DO value (mg/L) (ET/0510/012)	DO meter reading (mg/L)	Difference of DO Content (mg/L)
2	6.55	6.35	0.20
5	3.89	3.72	0.17
10	2.20	2.10	0.10

Criteria: Difference between DO meter reading and expected DO value: $< \pm 0.30\text{ mg/L}$

Salinity Checking by APHA 19ed 2520 B


	Expected Salinity (ppt)	DO meter reading (ppt)
Reagent No. of NaCl (10 ppt): CPE/012/4.7/27	10	9.6
Reagent No. of NaCl (30 ppt): CPE/012/4.8/27	30	28.5

Criteria: Difference between DO meter reading and expected Salinity: $\pm 10.0\%$

The equipment complies [#] / ~~does not comply~~ [#] with the specified requirements and is deemed acceptable [#] / unacceptable [#] for use.

[#] Delete as appropriate

Calibrated by : 

Approved by : 

Appendix F2

Impact Water Quality Monitoring Results

Impact Water Quality Monitoring

Monitoring Station: R1b

Date	Sampling Duration	Weather Condition	Sampling Level	Turbidity (NTU)			Dissolved Oxygen (DO) (mg/L)			Suspended Solid (SS) (mg/L)		
				1	2	Ave.	1	2	Ave.	1	2	Ave.
03/01/19	12:50-12:55	Cloudy	Mid-Depth	7.1	7.0	7.0	2.20	2.17	2.19	<5	<5	<5
05/01/19	14:00-14:05	Cloudy	Mid-Depth	8.9	8.9	8.9	2.07	2.04	2.06	<5	<5	<5
08/01/19	14:00-14:05	Cloudy	Mid-Depth	7.1	7.1	7.1	2.57	2.59	2.58	<5	<5	<5
10/01/19	13:00-13:05	Cloudy	Mid-Depth	7.6	7.5	7.5	1.98	2.02	2.00	<5	<5	<5
12/01/19	14:15-14:20	Cloudy	Mid-Depth	12.5	12.8	12.7	2.37	2.35	2.36	<5	<5	<5
15/01/19	13:00-13:05	Drizzle	Mid-Depth	3.7	3.8	3.7	2.82	2.79	2.81	<5	<5	<5
17/01/19	13:45-13:50	Cloudy	Mid-Depth	10.7	10.5	10.6	1.97	1.99	1.98	<5	<5	<5
19/01/19	09:10-09:15	Cloudy	Mid-Depth	5.6	5.5	5.6	2.17	2.20	2.19	<5	<5	<5
22/01/19	13:02-13:12	Cloudy	Mid-Depth	13.4	13.5	13.5	2.68	2.64	2.66	<5	<5	<5
24/01/19	13:00-13:05	Fine	Mid-Depth	7.4	7.5	7.4	2.02	2.05	2.04	7	7	7
26/01/19	13:29-13:39	Cloudy	Mid-Depth	8.3	8.3	8.3	2.87	2.89	2.88	<5	<5	<5
29/01/19	13:15-13:20	Fine	Mid-Depth	5.9	5.9	5.9	2.21	2.24	2.23	<5	<5	<5
31/01/19	13:55-14:08	Cloudy	Mid-Depth	6.9	6.8	6.8	2.97	3.00	2.99	<5	<5	<5
				Min		3.7	Min		1.97	Min		<5
				Max		13.5	Max		3.00	Max		7
				Average		8.1	Average		2.38	Average		1


Remark(s):

- (#) 200ml sample was used for Suspended Solids analysis. Practical Quantitation Limit of Suspended Solids reported less than 5 mg/L. The results reported as <5 would be counted as zero for average measurement.


Appendix F3

Graphical Plots of Impact Water Quality Monitoring Data


Impact Turbidity Result

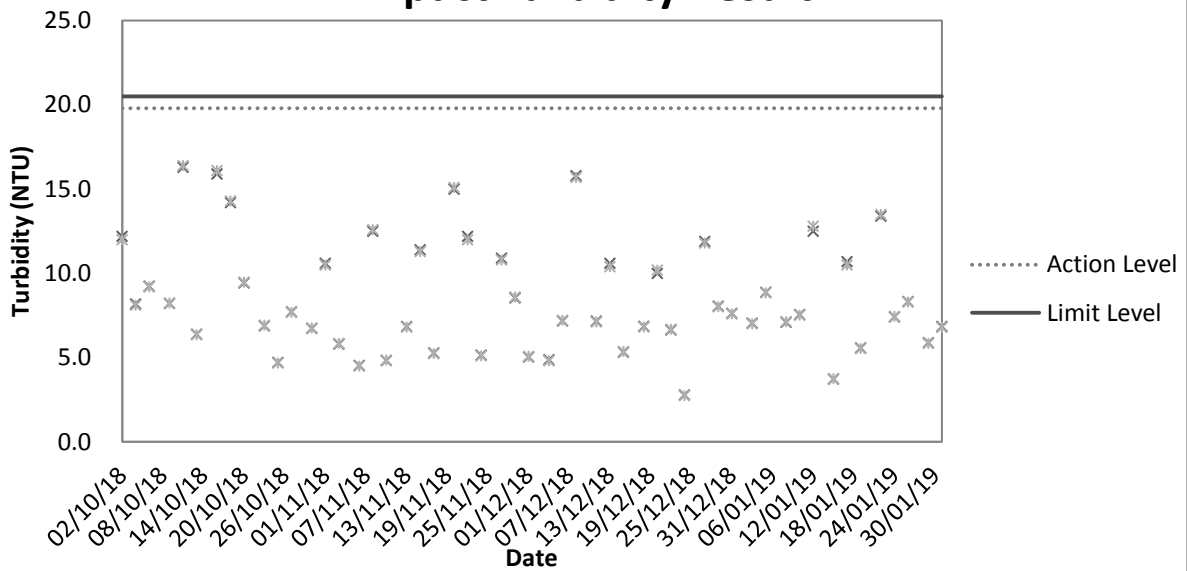

Impact DO Result

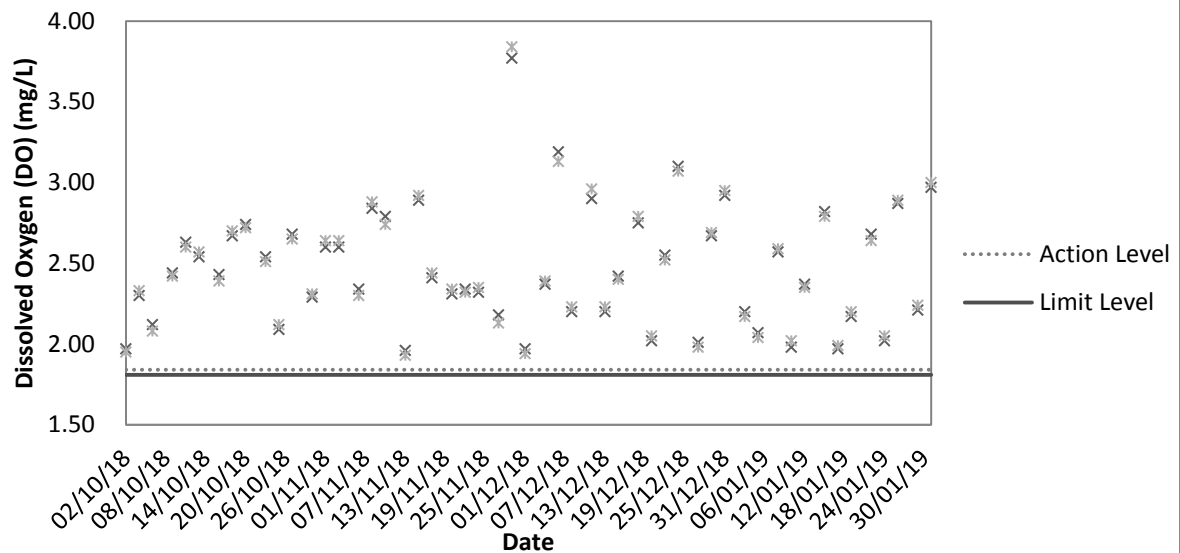

Impact Suspended Solid (SS) Result

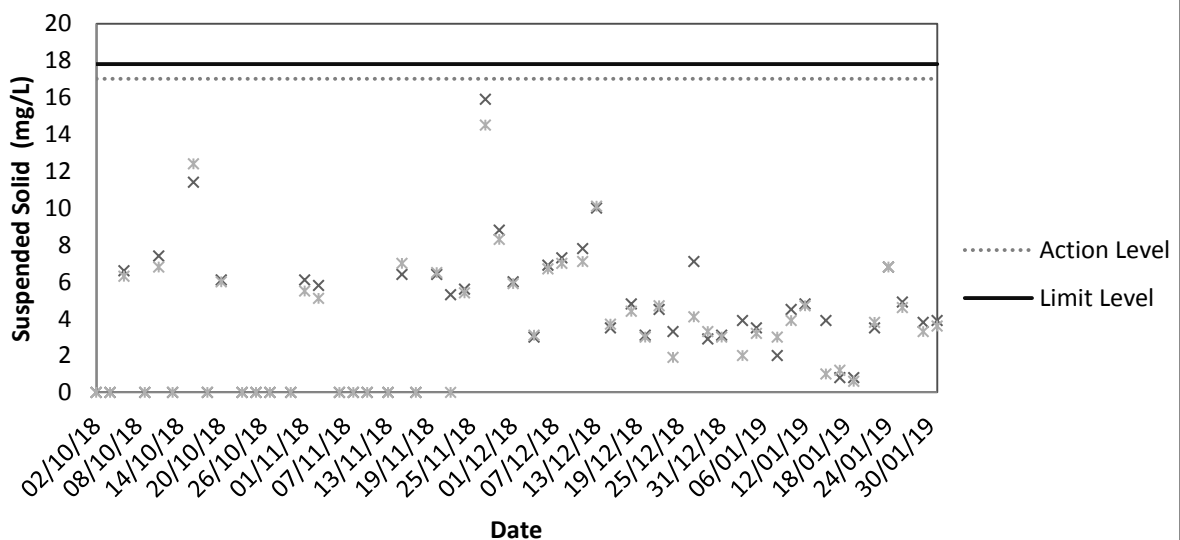

Appendix G

Weather Condition



Daily Extract of Meteorological Observations, January 2019 – Wetland Park

Day	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Total Rainfall (mm)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)					
01	1027.7	15.6#	12.0	9.1#	7.6	75	0.0	360	6.8
02	1026.5	16.2	13.3	11.1	8.6	74	0.0	350	5.9
03	1025.2	15.3	13.8	12.4	11.2	85	0.0	060	6.0
04	1023.0	21.1	17.7	14.5	16.0	90	0.5	270	3.1
05	1021.0	22.5	18.9	17.2	17.5	92	0.0	320	2.9
06	1022.1	19.4#	17.4	16.2#	14.2	82	0.0	060	6.2
07	1021.4	20.4#	18.1	16.5#	16.2	89	0.0	050	2.4
08	1021.5	21.1#	19.0	17.8#	15.8	82	0.0	340	3.2
09	1022.4	23.6#	18.3	16.2#	14.5	79	0.0	060	6.3
10	1020.2	24.0#	19.9	17.1#	16.9	83	0.0	050	4.9
11	1018.6	27.0	21.0	17.1	18.7	88	0.0	330	2.7
12	1018.4	23.2	20.3	17.8	18.0	87	0.0	320	2.8
13	1019.2	21.1	19.3	17.8	17.6	90	0.0	060	5.7
14	1018.6	21.7#	19.3	17.6#	17.0	87	0.0	060	5.0
15	1019.1	22.3	19.0	17.1	17.1	89	6.0	040	4.1
16	1021.4	19.2#	16.2	14.4#	10.7	70	0.0	020	8.8
17	1022.7	21.9#	16.0	13.1#	9.8	67	0.0	050	6.3
18	1022.5	19.2#	16.1	12.7#	11.2	73	0.0	060	5.0
19	1019.6	24.3#	19.1	14.9#	15.1	79	0.0	060	4.0
20	1018.9	25.6#	20.8	17.6#	16.4	77	0.0	060	3.7
21	1022.4	21.0#	17.0	14.9#	10.0	63	0.0	010	7.7
22	1022.9	20.0	14.6	10.9	5.7	57	0.0	340	5.6
23	1021.3	21.0#	14.8	9.4#	6.8	62	0.0	060	3.4
24	1020.5	22.0#	15.6	10.8#	11.2	79	0.0	310	3.5
25	1021.3	25.7#	17.4	12.3#	12.5	76	0.0	010	2.8
26	1023.1	24.2#	17.8	14.1#	11.6	70	0.0	050	4.0
27	1023.5	21.7#	16.7	13.7#	11.9	75	0.0	040	4.8
28	1021.6	22.7#	17.2	13.5#	11.5	72	0.0	060	4.5
29	1021.3	23.4#	17.9	12.5#	11.9	72	0.0	060	5.8
30	1020.7	23.9#	18.0	12.9#	14.5	82	0.0	060	3.5
31	1019.2	26.7#	20.8	15.6#	17.2	82	0.0	320	3.2

Remark(s):

1. # data incomplete
2. Rainfall measured in increment of 0.5 mm. Amount of < 0.5 mm cannot be detected
3. The meteorological observations extracted from Hong Kong Observatory only shown the daily average and may be varied from the weather condition recorded during monitoring.

Appendix H

Environmental Site Inspection Checklist

Environmental Site Inspection Checklist – San Wai

Inspection Date: 4. 1. 19 Inspected By: Frankie Tang
 Time: 14:00 Weather Condition: Fine
 Participants: Patrick Leung, Johnny So, Jackson Leung, Abby Sharn

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <u>Not observed</u>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding $\geq 2.4\text{m}$ tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	Construction Activities				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	item 1
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit: N/A

Observations ItnI: Stagnant water was observed at Portion P1

Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

To clean the stagnant water properly.

Signature:

ET's representative

Name: Tony Ching Hy
Date: 4.1.19

Signature:

ET Leader

Name: C. L. Lau
Date: 5.1.19

Signature:

Contractor's representative


Name: Leung Chi Kit
Date: 4.1.19


Signature:

SO's representative

Name: C. F. Chan
Date: 4/1/2019

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 27/12/2018, chemical containers were removed.</p>	--	190104_001	No	--

1	 <p>Stagnant water was observed at Portion P1.</p>	To clear the stagnant water properly.	190104_002	Yes	11/01/2019
---	--	---------------------------------------	------------	-----	------------



Environmental Site Inspection Checklist – San Wai

Inspection Date: 11 January 2018 Inspected By: Ivy Lo
Time: 09:30 Weather Condition: Fine
Participants: Patrick Leung, Johnny So, Jason Leung, Abby Sham

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <u>Not observed</u>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding ≥ 2.4 m tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit:

~~NA~~ Follow up action to item on 07/01/2018,
all item was improved.

Observations


No adverse observation was recorded
during this site inspection.

Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

NA


Signature:

ET's representative


Name: Ivy Lo
Date: 11/1/2019


Signature:

Contractor's representative


Name: Larry Ch. Kit
Date: 11/1/19


Signature:

ET Leader



Name: C. L. Lam
Date: 12/1/2018

Signature:

SO's representative


Name: O F Goh
Date: 11/1/2019

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 04/01/2019, stagnant water was cleared at Portion P1.</p>	--	190111_001	No	--



Environmental Site Inspection Checklist – San Wai

Inspection Date:

18.1.19

Inspected By:

Frankie Tng

Time:

14:00

Weather Condition:

Fine

Participants:

Patrick Lam, Johnny So, Telly Tunn, Kevin Tng

		N/A	Yes	No	Remarks
1	Permits/Licenses				
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality				
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <i>not shown</i>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding $\geq 2.4\text{m}$ tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	Construction Activities				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	item 2
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5	Waste / Chemical Management	N/A	Yes	No	Remarks
	General Waste				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	Construction Waste				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	




Follow up actions for pervious Site Audit: N/A

Observations Ith I: Chemical wastes area was found without chemical label.


Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

Ith I: Provide the chemical label properly.


Signature:
ET's representative


Name: Tony Ching Hing
Date: 18.1.19


Signature:
ET Leader


Name: C. H. Lan
Date: 18.1.19


Signature:
Contractor's representative


Name: Leung Chi Kit
Date: 18.1.19

Signature:
SO's representative


Name: C. F. Fong
Date: 18/1/2019

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
1	 <p>Chemical wastes area was found without chemical label.</p>	To provide correct chemical label for the chemical wastes area.	190118_001	Yes	25/01/2019


Environmental Site Inspection Checklist – San Wai

Inspection Date: 25-1-19 Inspected By: Frankie Tong
 Time: 14:00 Weather Condition: Fine
 Participants: Patrick Leung, Johnny So, Jackson Leung, Abby Shum

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <u>Not observed</u>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding ≥ 2.4 m tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	Construction Activities				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	if not
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit: Follow up action to item on 18-1-19, all item was improved

Observations


Item 1: Water quality of wetsep tank should be improved

Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

Item 1: To clean the accumulated mud at wetsep tank properly


Signature:

ET's representative


Name: Tang Ching Hong
Date: 25-1-19


Signature:

Contractor's representative


Name: Leung Chi Kit
Date: 25-1-19


Signature:

ET Leader




Name: C. L. Lau
Date: 26-1-19

Signature:

SO's representative


Name: C. F. Chan
Date: 28/1/2019

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 18/01/2019, correct chemical label was provided.</p>	--	190125_001	No	--
1	 <p>Water quality of Wetsep Tank should be improved.</p>	To clean the accumulated mud inside the Wetsep Tank properly	190125_002	Yes	30/01/2019



Environmental Site Inspection Checklist – San Wai

Inspection Date: 30.1.19 Inspected By: Frankie Tang
 Time: 14:00 Weather Condition: Fine
 Participants: Patrick Lam, Johnny So, Jackson Lam, Abby Shun

		N/A	Yes	No	Remarks
1	Permits/Licenses				
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality				
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <u>Not Observed</u>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding $\geq 2.4\text{m}$ tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
Chemical / Fuel Storage Area					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
Chemical Waste / Waste Oil					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
Records					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit: Follow up action to item on 25-1-19, all item was improved

Observations

N/A

Corrective Actions – Mitigation Measures Implemented or Proposed (if any): N/A

Signature:

ET's representative

Name: Tay Chy Hing
Date: 30-1-19

Signature:

Contractor's representative

Name: Leung Chi Kit
Date: 30-1-19

Signature:

ET Leader


Name: C-h. Lan
Date: 31.1.19

Signature:

SO's representative

Name: C7 BAKH
Date: 30/1/2019

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 25/01/2019, accumulated mud was cleaned.</p>	--	190130_001	No	--

Appendix I

Landscape and Visual Impact Assessment Checklist

Landscape and Visual Impact Assessment Checklist for Site Audit

Inspection Date: 11 January 2019 **Weather:** Sunny/~~Fine~~/~~Cloudy~~/~~Rainy~~
Time: 15:30 p.m. **Wind:** Strong/~~Breeze~~/~~Light~~/~~Calm~~

Item	Description	YES	NO	N/A	Actions/ Remarks
1	Construction Phase				
1.1	Is the detailed tree survey completed prior to construction work?	✓			
1.2	Are trees to be transplanted removed to their final positions?		✓		
1.3	Are the transplants and existing trees to be retained properly protected from damage by stout hoarding positioned as directed by a qualified Landscape Architect?	✓			Eastern side trees: Protective fence has been provided at lot. Northern side trees: They are protected outside lot.
1.4	Is regular inspection of the retained and transplanted trees made to ensure the effectiveness of the hoarding?	✓			
1.5	Are the TPZ clearly demarcated on site and surrounded by strong fences sturdy enough to withstand impacts from the construction activities?	✓			Except trees far beyond the extent of construction activities, strong protective fence is noted. Eastern side trees: Protective fence has been provided at lot. Northern side trees: They are protected outside lot.
1.6	Are warning signs and notices installed at the fences denoting the “tree protection zone” to prohibit the entry of equipment or construction activities?	✓			
1.7	Are tree labels with clear indication of tree no. and status (e.g. “R”, “T” or “F”) provided for all the trees on site?	✓			
1.8	If protective fencings are not practicable, are the tree root systems adequately protected from soil compaction due to passage of vehicles, equipment or machinery?	✓			

1.9	Are vehicular/foot paths and storage areas designated away from TPZ?	✓			
1.10	Are the trees properly irrigated and sprayed with water to remove the accumulated construction dust during dry season in order to lessen the chances of decline and to maintain the vigour of trees?			✓	
1.11	Are the trees free from any sign of distress, such as dieback, leaf loss, or general decline in tree health or appearance or tree damage with symptoms of construction injury?			✓	Trees in eastern boundary: 1) Dead branches to remove 2) Tear bark/ stubs to be properly primed.
1.12	Are the trees free from wire or nail and prohibited to be used as anchor for any site activities?	✓			
1.13	Are cutting, trenching, excavating or raising of soil level within the TPZ prohibited?	✓			
1.14	Is improper pruning of the tree branches/roots prohibited?	✓			
1.15	Are the trees free from any tree root damage?	✓			
1.16	Are construction works or operation of machines within the TPZ prohibited?	✓			
1.17	Is the TPZ free from pollution from effluent water, machine petroleum or chemical spillage?	✓			
1.18	Is the excavated topsoil stored and protected on site for reuse for restoration of screen planting works?			✓	The site has previously been reclaimed from ponds. Most of the excavated topsoil is not desirable for reuse due to its inferior quality. Contractor's submitted referencing documents are attached in the checklist dated 4 May, 2018 for information.
1.19	Is the progress of the above activities reported in the monthly EM&A report?	✓			
2	Operational Phase (12 months period from commissioning of the expanded and upgraded works)				

2.1	Is a planting reserve, where locates around the site perimeter of approximately 5m wide, provided to allow a continuous belt of trees to be planted as a visual screen?			✓	
2.2	Is the planting reserve complemented the boundary planting to the existing San Wai STW?			✓	
2.3	Is all new planting maintained for 12 months to ensure proper establishment?			✓	
2.4	Are the trees free from sign of deterioration of tree health and/or structure?			✓	
2.5	Are the trees free from insect pests and disease pathogens?			✓	
2.6	Are the irrigation systems functioning properly and well maintained?			✓	
2.7	Are the tree root systems adequately protected from soil compaction due to storage of materials or operation of machinery?			✓	

Summary/ Remarks:

Follow up actions taken by Contractor for previous comments:

1. Trees at eastern boundary – pruning of dead branches has carried out. Contractor is reminded to carry out proper reduction cut to some of the branches in future to meet the current tree care standard.

The contractor was reminded to rectify the following:

1. Generally, contractor was reminded to keep on the tree protection and maintenance.

New Observation:

1. Grade change and construction activities are noted on site. Contractor was reminded not to disturb the TPZ.

Reminders:

1. Contractor was reminded to provide TPZ with robust fence, whenever possible, at the drip line of all retained trees unless the trees are well beyond the extend of construction activities.

Photo Record:




Figure 1	Figure 2
	
General condition of the tress at northern side of the site	General condition of the trees at south-west corner of the site

Figure 3	Figure 4
	
<p>General condition of the existing trees at eastern boundary</p>	<p>General condition of the existing trees at eastern boundary</p>
Figure 5	Figure 6
	
<p>Condition of trees at the entrance of the existing treatment plant</p>	<p>Protective fence (outside works extent) is needed</p>

Signature:

		Signature	Date
Inspected & Recorded by	Registered Landscape Architect		
		Xylem Leung	

Landscape and Visual Impact Assessment Checklist for Site Audit

Inspection Date: 25 January 2019 **Weather:** Sunny/ Fine/ Cloudy/ Rainy
Time: 14:30 p.m. **Wind:** Strong/ Breeze/ Light/ Calm

Item	Description	YES	NO	N/A	Actions/ Remarks
1	Construction Phase				
1.1	Is the detailed tree survey completed prior to construction work?	✓			
1.2	Are trees to be transplanted removed to their final positions?		✓		
1.3	Are the transplants and existing trees to be retained properly protected from damage by stout hoarding positioned as directed by a qualified Landscape Architect?	✓			<p>Eastern side trees: Protective fence has been provided at lot.</p> <p>A few nos. of trees are protected near the site entrance</p>
1.4	Is regular inspection of the retained and transplanted trees made to ensure the effectiveness of the hoarding?	✓			
1.5	Are the TPZ clearly demarcated on site and surrounded by strong fences sturdy enough to withstand impacts from the construction activities?	✓			Except trees far beyond the extent of construction activities, protective fence is noted.
1.6	Are warning signs and notices installed at the fences denoting the “tree protection zone” to prohibit the entry of equipment or construction activities?	✓			
1.7	Are tree labels with clear indication of tree no. and status (e.g. “R”, “T” or “F”) provided for all the trees on site?	✓			
1.8	If protective fencings are not practicable, are the tree root systems adequately protected from soil compaction due to passage of vehicles, equipment or machinery?	✓			
1.9	Are vehicular/foot paths and storage areas designated away from TPZ?	✓			
1.10	Are the trees properly irrigated and sprayed with water to remove the accumulated construction dust during dry season in order to lessen the chances of decline and to			✓	

	maintain the vigour of trees?				
1.11	Are the trees free from any sign of distress, such as dieback, leaf loss, or general decline in tree health or appearance or tree damage with symptoms of construction injury?			✓	Trees in eastern boundary: 1) Dead branches to remove 2) Tear bark/ stubs to be properly pruned.
1.12	Are the trees free from wire or nail and prohibited to be used as anchor for any site activities?	✓			
1.13	Are cutting, trenching, excavating or raising of soil level within the TPZ prohibited?	✓			
1.14	Is improper pruning of the tree branches/roots prohibited?	✓			
1.15	Are the trees free from any tree root damage?	✓			
1.16	Are construction works or operation of machines within the TPZ prohibited?	✓			
1.17	Is the TPZ free from pollution from effluent water, machine petroleum or chemical spillage?	✓			
1.18	Is the excavated topsoil stored and protected on site for reuse for restoration of screen planting works?			✓	The site has previously been reclaimed from ponds. Most of the excavated topsoil is not desirable for reuse due to its inferior quality. Contractor's submitted referencing documents are attached in the checklist dated 4 May, 2018 for information.
1.19	Is the progress of the above activities reported in the monthly EM&A report?	✓			
2	Operational Phase (12 months period from commissioning of the expanded and upgraded works)				
2.1	Is a planting reserve, where locates around the site perimeter of approximately 5m wide, provided to allow a continuous belt of trees to be planted as a visual screen?			✓	
2.2	Is the planting reserve complemented the boundary planting to the existing San Wai			✓	

	STW?				
2.3	Is all new planting maintained for 12 months to ensure proper establishment?			✓	
2.4	Are the trees free from sign of deterioration of tree health and/or structure?			✓	
2.5	Are the trees free from insect pests and disease pathogens?			✓	
2.6	Are the irrigation systems functioning properly and well maintained?			✓	
2.7	Are the tree root systems adequately protected from soil compaction due to storage of materials or operation of machinery?			✓	

Summary/ Remarks:

Follow up actions taken by Contractor for previous comments:

1. Trees at eastern boundary – pruning of dead branches has carried out. Contractor is reminded to carry out proper reduction cut to some of the branches in future to meet the current tree care standard.

The contractor was reminded to rectify the following:

1. Generally, contractor was reminded to keep on the tree protection and maintenance.

New Observation:

1. Grade change and construction activities are noted on site. Contractor was reminded not to disturb the TPZ.

Reminders:

1. Contractor was reminded to provide TPZ with robust fence, whenever possible, at the drip line of all retained trees unless the trees are well beyond the extend of construction activities.

Photo Record:



Figure 1	Figure 2
	
<p>General condition of the existing trees at eastern boundary</p>	<p>General condition of the south-west corner of the site. Former trees are removed.</p>

Figure 3




Condition of trees at the entrance of the existing treatment plant

Figure 4




All the existing trees near the eastern entrance are removed

Figure 5

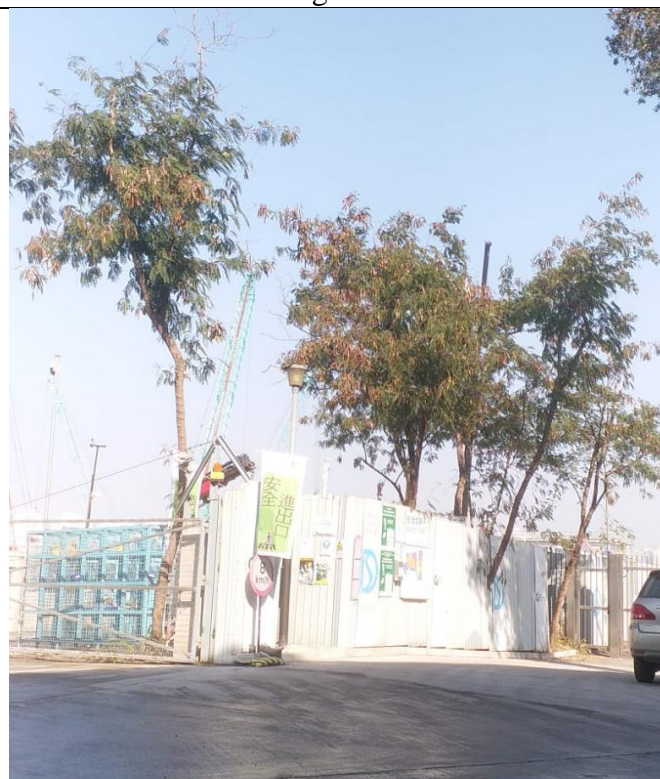

Existing trees at the site entrance protected by the hoarding fence

Signature:

		Signature	Date
Inspected & Recorded by	Registered Landscape Architect		
		Xylem Leung	

Appendix J

Waste Flow Table

DSD Contract: DC/2013/10
Design, Build and Operate
San Wai Sewage Treatment Works Phase 1



ATAL-Degremont-China Harbour Joint Venture

Name of Department: DSD

Year: 2019

Project: Design, Build and Operate San Wai Sewage Treatment Works - Phase 1

Contract No.: DC/2013/10

Waste Flow Table

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Broken Concrete (see Note ³)	Reused in the Contract (see Note)	Reused in other Projects	Disposed as Public Fill (see Note ⁴)	Imported Fill (see Note ⁴)	Metals	Paper/ cardboard packaging	Plastics (see Note ²)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 kg)
Jan	0.988	0.000	0.000	0.000	0.988	0.449	0.000	0.000	0.000	0.000	55.820
Feb											
Mar											
Apr											
May											
Jun											
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	0.988	0.000	0.000	0.000	0.988	0.449	0.000	0.000	0.000	0.000	55.820

Notes: (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.

(2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.

(3) Broken concrete for recycling into aggregates.

(4) Assumption: The densities of subbase, Type A, Type B, Rockfill, Soil, Mix Rock and Soil, Reclaimed Asphalt Pave, Slurry are 2.0 ton/m³; the densities of Building debris and special fill materials are 2.1 ton/m³; the densities of Broken Concrete is 2.4 ton/m³.

Appendix K

Environmental Licenses and Permits

Item No.	Nature of Permit / License / Notification	Permit / License/ Notification No.	Date of Issue / Effective of Permit / License	Date of Expiry of Permit / License	Remark (Validity for reporting period only)
1	Environmental Permit	EP-464/2013	18/10/2013	NA	Valid
2	Billing Account for Disposal of Construction Waste	7025330	07/07/2016	NA	Valid
3	Form NA notification (for APCO)	405489	26/07/2016	25/09/2020	Valid
4	Chemical Waste Producer Registration (for Site)	5218-511-A2823-01	23/01/2017	NA	Valid
5	Wastewater Discharge Licence (for WPCO)	WT00026754-2017	28/04/2017	31/01/2022	Valid
6	Construction Noise Permit (for Site)	GW-RN0698-19	13/12/2018	12/06/2019	Valid

Appendix L

Implementation Schedule for Environmental Mitigation Measures (EMIS)

Environmental Mitigation Measures	Location	Implementation Status			
		Implemented	Partially implemented	Not implemented	Not Applicable
Air Quality					
<ul style="list-style-type: none">The working area for the uprooting of trees, shrubs, or vegetation or for the removal of boulders, poles, pillars or temporary or permanent structures should be sprayed with water or a dust suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;	Site Area	√			
<ul style="list-style-type: none">All demolished items (including trees, shrubs, vegetation, boulders, poles, pillars, structures, debris, rubbish and other items arising from site clearance) that may dislodge dust particles should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition;	Site Area	√			
<ul style="list-style-type: none">Vehicle washing facilities including a high pressure water jet should be provided at every discernible or designated vehicle exit point;	Site Entrance	√			
<ul style="list-style-type: none">The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;	Site Exit	√			
<ul style="list-style-type: none">Where a site boundary adjoins a road, street, service and or other area accessible to the public, hoarding of not less than 2.4m from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit;	Site Area	√			
<ul style="list-style-type: none">Every main haul road (i.e. any course inside a construction site having a vehicle passing rate of higher than 4 in any 30 minutes) should be paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical so as to maintain the entire road surface wet;	Main Haul Road	√			
<ul style="list-style-type: none">The portion of any road leading only to a construction site that is within 30m of a discernible or designated vehicle entrance or exit should be kept clear of dusty materials;	Site Entrance and Exit	√			
<ul style="list-style-type: none">Immediately before leaving a construction site, every vehicle should be washed to remove any dusty materials from its body and wheels;	Site Exit	√			
<ul style="list-style-type: none">Where a vehicle leaving a construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle;	--	√			
<ul style="list-style-type: none">The working area of any excavation or earth moving operation should be sprayed with water or a dusty suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;	Site Area	√			
<ul style="list-style-type: none">Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable	Site Area	√			

surface stabilizer within 6 months after the last construction activity on the construction site or part of the construction site where the exposed earth lies;					
• Any stockpile of dusty material should be either covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or a dust suppression chemical so as to maintain the entire surface wet.	Site Area	√			
Noise					
• Quiet plants should be used in order to reduce the noise impacts to protect the nearby NSRs.	Site Area	√			
• Temporary and Movable Noise Barriers should be used in order to reduce the noise impact to the surrounding sensitive receivers	Site Area	√			
• Intermittent noisy activities should be scheduled to minimize exposure of nearby NSRs to high levels of construction noise.	Site Area	√			
• Idle equipment should be turned off or throttled down.	Site Area	√			
• Construction activities should be planned so that parallel operation of several sets of equipment close to a given receiver is avoided	Site Area	√			
• Construction plant should be properly maintained and operated.	Site Area	√			
Water Quality					
• Exposed stockpiles should be covered with tarpaulin or impervious sheets before a rainstorm occurs;	Site Area	√			
• The exposed soil surfaces should also be properly protected to minimize dust emission;	Site Area	√			
• The stockpiles of materials should be placed in the locations away from the drainage channel so as to avoid releasing materials into the channel;	Site Area	√			
• Wheel washing facilities should be provided at site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles;	Site Exit	√			
• Provision of site drainage systems and treatment facilities would be required to minimize the water pollution;	Site Area		√		
• A discharge license needs to be applied from EPD for discharging effluent from the construction site;	--	√			
• The treated effluent quality is required to meet the requirements specified in the discharge license;	--	√			
• Provision of chemical toilets is required to collect sewage from workforce. The chemical toilets should be cleaned on a regular basis;	Chemical Toilet	√			

• A licensed waste collector should be employed to clean the chemical toilets and temporary storage tank on a regular basis;	--	√			
• Illegal disposal of chemicals should be strictly prohibited;	Site Area	√			
• Registration as a chemical waste producer is required if chemical wastes are generated and need to be disposed of. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes;	Site Area	√			
• Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance should be used as a guideline for handling chemical wastes;	Site Area		√		
• The impact from accidental spillage of chemicals can be effectively controlled through good management practices.	Site Area	√			
Waste Management					
• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;	Site Area	√			
• To encourage collection of aluminium cans by individual collectors, separate bins should be provided to segregate this waste from other general refuse generated by the workforce;	Site Area	√			
• Any unused chemicals or those with remaining functional capacity should be recycled;	Site Area	√			
• Prior to disposal of C&D waste, it is recommended that wood, steel and other metals be separated for re-use and/or recycling and inert waste as fill material to minimize the quantity of waste to be disposed of to landfill;	Site Area	√			
• Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and	Site Area		√		
• Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.	Site Area	√			
Landscape and Visual					
• Detailed tree survey should have been completed	Site Area	√			
• Trees should be transplanted to their final positions clear of the construction site	--			√	
• Erect site hoarding to protect adjacent vegetation from damage	Site Area	√			

<ul style="list-style-type: none"> Regular inspections of the transplanted trees should be made to ensure the effectiveness of the hoarding 	Site Area	√			
<ul style="list-style-type: none"> Any topsoil excavated during the course of the works should be stored and protected on site for reuse for the restoration and screen planting works 	Site Area			√	

Appendix M


Environmental Site Inspection Schedule

Contract No. DC/2013/10 -
Design, Build and Operate San Wai Sewage Treatment Works – Stage 1
Schedule for Environmental Monitoring and Site Inspection
January 2019

Sun	Mon	Tue	Wed	Thu	Fri	Sat
		1	2	3 Effluent Sampling	4 24hr-TSP 1hr-TSP x 3 NM SI	5
6	7	8 WQM	9	10 24hr-TSP 1hr-TSP x 3 NM WQM	11 SI	12 WQM
13	14	15 Effluent Sampling WQM	16 24hr-TSP 1hr-TSP x 3 NM	17 WQM	18 SI	19 WQM
20	21	22 24hr-TSP 1hr-TSP x 3 NM WQM	23	24 WQM	25 SI	26 WQM
27	28 24hr-TSP 1hr-TSP x 3 NM	29 Effluent Sampling WQM	30	31 WQM		

Appendix N

Laboratory Report for Discharge Water



東業德勤測試顧問有限公司 ETS-TESTCONSULT LTD.™

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: etl@ets-testconsult.com
W: www.ets-testconsult.com



TEST REPORT

Testing of Water and Wastewater

Report No. : ENA90637
Date of Issue : 17 January 2019
Page No. : 1 of 1

Information Provided by Customer

Customer Name : ATAL-Degremont-China Harbour Joint Venture
Customer Address : 19/F, China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of Sampling : 03 January 2019
Sample Description : Sample was stored in 1L plastic bottle (for pH and Total Suspended Solids).
Sample was stored in 500ml plastic bottle (for Chemical Oxygen Demand).
Sample for Chemical Oxygen Demand was preserved by adding conc. H₂SO₄ to pH <2.
Sample was collected by the customer and refrigerated after received.

Laboratory Information

Date of Received : 03 January 2019
Date of Testing Period : 03 to 07 January 2019
Lab Ref. No. : W43005

Result

Sample ID	Sample No.	Test	Method Used	Result	Unit
P1b	01	pH	In house method TPE/003/W	8.4	(at 25°C)
		Total Suspended Solids	In house method TPE/006/W	<5*	mg/L
	02	Chemical Oxygen Demand	In house method TPE/002/W	<10	mgO ₂ /L

Remark(s):

- The results relate only to the tested sample as received.
- *200ml sample was used for Total Suspended Solids analysis. PQL of Total Suspended Solids reported less than 5 mg/L.


Approved Signatory :

LAU, Chi Leung

TPE/001/W

HKAS has accredited this laboratory (Reg. No. HOKLAS 022) under HOKLAS for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. This report shall not be reproduced unless with prior written approval from this laboratory.

- END OF REPORT -



東業德勤測試顧問有限公司 ETS-TESTCONSULT LTD.™

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: eti@ets-testconsult.com
W: www.ets-testconsult.com



TEST REPORT

Testing of Water and Wastewater

Report No. : ENA91021
Date of Issue : 29 January 2019
Page No. : 1 of 1

Information Provided by Customer

Customer Name : ATAL-Degremont-China Harbour Joint Venture
Customer Address : 19/F, China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of Sampling : 15 January 2019
Sample Description : Sample was stored in 1L plastic bottle (for pH and Total Suspended Solids).
Sample was stored in 500ml plastic bottle (for Chemical Oxygen Demand).
Sample for Chemical Oxygen Demand was preserved by adding conc. H₂SO₄ to pH <2.
Sample was collected by the customer and refrigerated after received.

Laboratory Information

Date of Received : 15 January 2019
Date of Testing Period : 15 to 17 January 2019
Lab Ref. No. : W43128

Result

Sample ID	Sample No.	Test	Method Used	Result	Unit
P1a	01	pH	In house method TPE/003/W	8.4	(at 25°C)
		Total Suspended Solids	In house method TPE/006/W	<5*	mg/L
	04	Chemical Oxygen Demand	In house method TPE/002/W	<10	mgO ₂ /L

Remark(s):

- The results relate only to the tested sample as received.
- *200ml sample was used for Total Suspended Solids analysis. PQL of Total Suspended Solids reported less than 5 mg/L.


Approved Signatory :

LAU, Chi Leung

TPE/001/W

HKAS has accredited this laboratory (Reg. No. HOKLAS 022) under HOKLAS for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. This report shall not be reproduced unless with prior written approval from this laboratory.

- END OF REPORT -



東業德勤測試顧問有限公司 ETS-TESTCONSULT LTD.™

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: eti@ets-testconsult.com
W: www.ets-testconsult.com



TEST REPORT

Testing of Water and Wastewater

Report No. : ENA91022
Date of Issue : 29 January 2019
Page No. : 1 of 1

Information Provided by Customer

Customer Name : ATAL-Degremont-China Harbour Joint Venture
Customer Address : 19/F, China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of Sampling : 15 January 2019
Sample Description : Sample was stored in 1L plastic bottle (for pH and Total Suspended Solids).
Sample was stored in 500ml plastic bottle (for Chemical Oxygen Demand).
Sample for Chemical Oxygen Demand was preserved by adding conc. H_2SO_4 to pH <2.
Sample was collected by the customer and refrigerated after received.

Laboratory Information

Date of Received : 15 January 2019
Date of Testing Period : 15 to 17 January 2019
Lab Ref. No. : W43128

Result

Sample ID	Sample No.	Test	Method Used	Result	Unit
P1b	02	pH	In house method TPE/003/W	8.3	(at 25°C)
		Total Suspended Solids	In house method TPE/006/W	<5*	mg/L
	05	Chemical Oxygen Demand	In house method TPE/002/W	<10	mgO ₂ /L

Remark(s):

- The results relate only to the tested sample as received.
- *200ml sample was used for Total Suspended Solids analysis. PQL of Total Suspended Solids reported less than 5 mg/L.


Approved Signatory :

LAU, Chi Leung

TPE/001/W

HKAS has accredited this laboratory (Reg. No. HOKLAS 022) under HOKLAS for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. This report shall not be reproduced unless with prior written approval from this laboratory.

- END OF REPORT -



TEST REPORT

Testing of Water and Wastewater

Report No. : ENA91023
Date of Issue : 29 January 2019
Page No. : 1 of 1

Information Provided by Customer

Customer Name : ATAL-Degremont-China Harbour Joint Venture
Customer Address : 19/F, China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of Sampling : 15 January 2019
Sample Description : Sample was stored in 1L plastic bottle (for pH and Total Suspended Solids).
Sample was stored in 500ml plastic bottle (for Chemical Oxygen Demand).
Sample for Chemical Oxygen Demand was preserved by adding conc. H₂SO₄ to pH <2.
Sample was collected by the customer and refrigerated after received.

Laboratory Information


Date of Received : 15 January 2019
Date of Testing Period : 15 to 17 January 2019
Lab Ref. No. : W43128

Result

Sample ID	Sample No.	Test	Method Used	Result	Unit
P8	03	pH	In house method TPE/003/W	8.4	(at 25°C)
		Total Suspended Solids	In house method TPE/006/W	<5*	mg/L
	06	Chemical Oxygen Demand	In house method TPE/002/W	<10	mgO ₂ /L

Remark(s):

- The results relate only to the tested sample as received.
- *200ml sample was used for Total Suspended Solids analysis. PQL of Total Suspended Solids reported less than 5 mg/L.

Approved Signatory : 

LAU, Chi Leung


TPE/001/W

HKAS has accredited this laboratory (Reg. No. HOKLAS 022) under HOKLAS for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. This report shall not be reproduced unless with prior written approval from this laboratory.

- END OF REPORT -

Figure 1

Locations of Air Quality and Noise Monitoring Stations

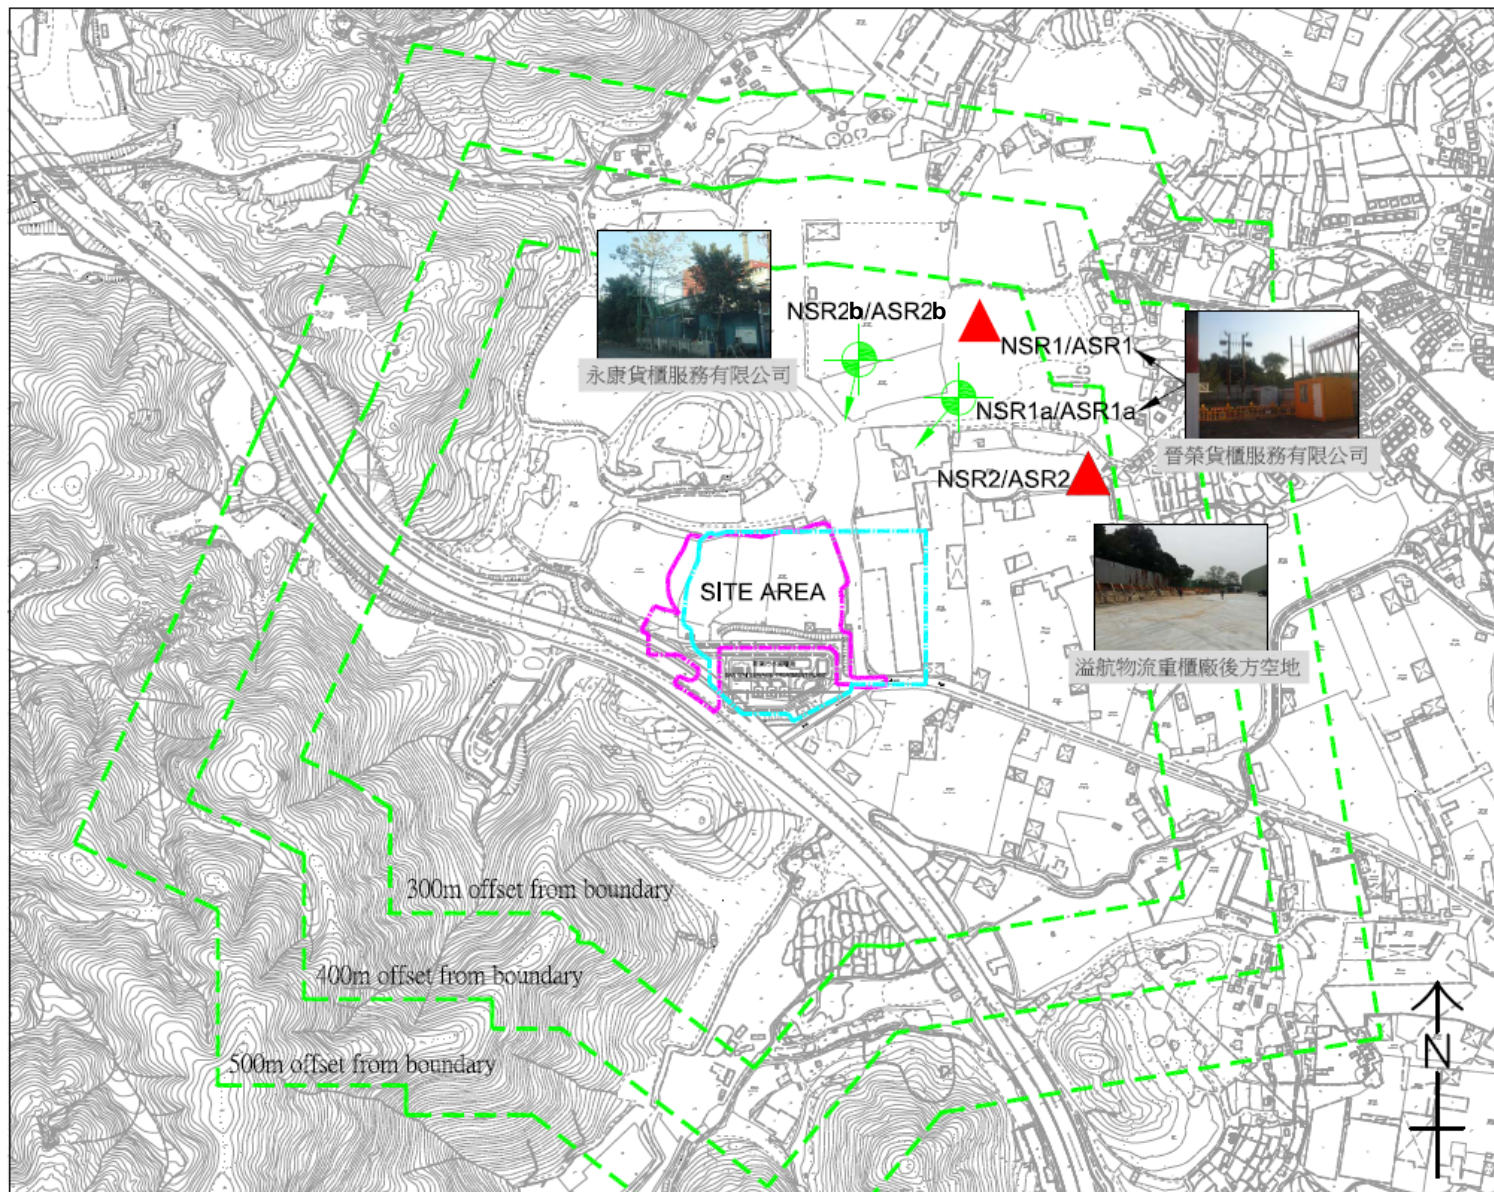


Project: Contract No. DC/2013/10 -Design, Build and Operate San Wai Sewage Treatment Works – Phase 1

Figure 1 Locations of Air Quality and Noise Monitoring Stations

Figure 2


Locations of Water Quality Monitoring Station

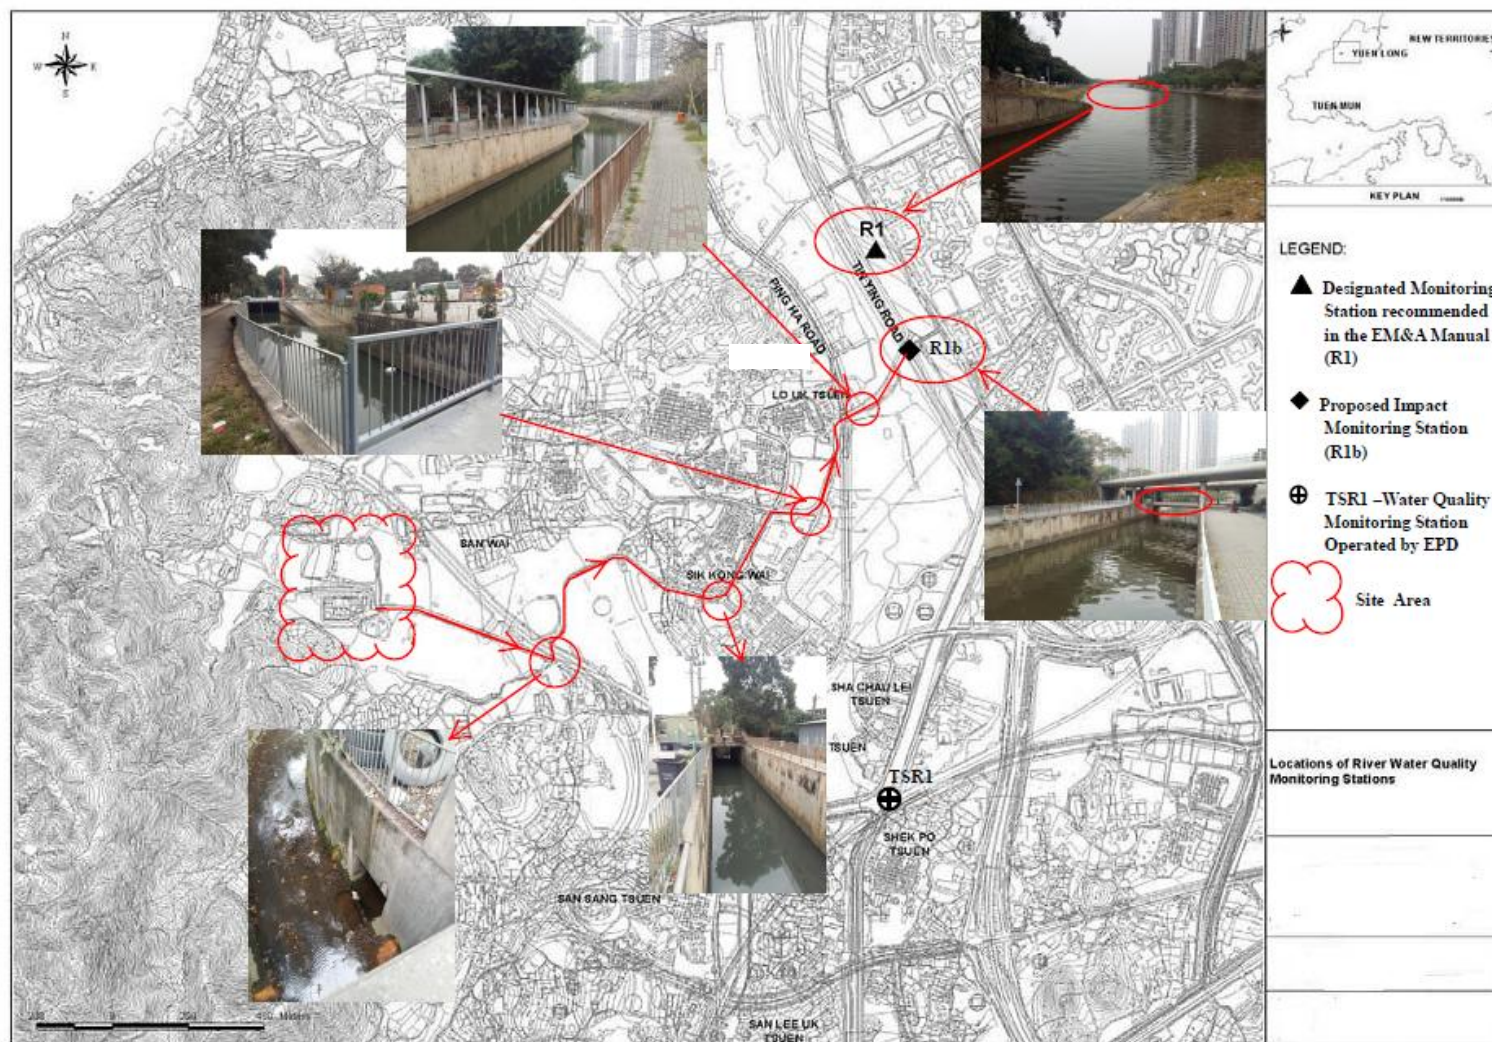

Project: Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Figure 2 Locations of Water Quality Monitoring Station

Figure 3

Location Plan for the Wetsep Treatment Tank

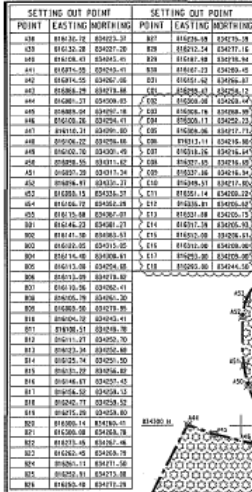

SETTING OUT POINT			
POINT	EASTING	NORTHING	
001	800827.50	870480.58	
002	800147.50	870475.55	
003	800446.56	870463.18	
004	800446.56	870463.18	
005	800446.56	870463.18	
006	800520.81	870463.18	
007	800446.56	870463.18	
008	800446.56	870463.18	
009	800446.56	870463.18	
010	800446.56	870463.18	
011	800446.56	870463.18	
012	800446.56	870463.18	
013	800446.56	870463.18	
014	800446.56	870463.18	
015	800446.56	870463.18	
016	800446.56	870463.18	
017	800446.56	870463.18	
018	800446.56	870463.18	
019	800446.56	870463.18	
020	800446.56	870463.18	
021	800446.56	870463.18	
022	800446.56	870463.18	
023	800446.56	870463.18	
024	800446.56	870463.18	
025	800446.56	870463.18	
026	800446.56	870463.18	
027	800446.56	870463.18	
028	800446.56	870463.18	
029	800446.56	870463.18	
030	800446.56	870463.18	
031	800446.56	870463.18	
032	800446.56	870463.18	
033	800446.56	870463.18	
034	800446.56	870463.18	
035	800446.56	870463.18	
036	800446.56	870463.18	
037	800446.56	870463.18	
038	800446.56	870463.18	
039	800446.56	870463.18	
040	800446.56	870463.18	
041	800446.56	870463.18	
042	800446.56	870463.18	
043	800446.56	870463.18	
044	800446.56	870463.18	
045	800446.56	870463.18	
046	800446.56	870463.18	
047	800446.56	870463.18	
048	800446.56	870463.18	
049	800446.56	870463.18	
050	800446.56	870463.18	
051	800446.56	870463.18	
052	800446.56	870463.18	
053	800446.56	870463.18	
054	800446.56	870463.18	
055	800446.56	870463.18	
056	800446.56	870463.18	
057	800446.56	870463.18	
058	800446.56	870463.18	
059	800446.56	870463.18	
060	800446.56	870463.18	
061	800446.56	870463.18	
062	800446.56	870463.18	
063	800446.56	870463.18	
064	800446.56	870463.18	
065	800446.56	870463.18	
066	800446.56	870463.18	
067	800446.56	870463.18	
068	800446.56	870463.18	
069	800446.56	870463.18	
070	800446.56	870463.18	
071	800446.56	870463.18	
072	800446.56	870463.18	
073	800446.56	870463.18	
074	800446.56	870463.18	
075	800446.56	870463.18	
076	800446.56	870463.18	
077	800446.56	870463.18	
078	800446.56	870463.18	
079	800446.56	870463.18	

NOTES:

1. ALL PLANNING CO-ORDINATES TO HONG KONG CHRON LAND AND SURVEY OFFICE METRIC GRID TWO BAKAN.
2. ALL LEVELS TO HONG KONG CHRON LAND AND SURVEY OFFICE PINGTUNG CURVA.
3. ALL QUITS ARE TO MILLIMETERS UNLESS SPECIFIED OTHERWISE.
4. THE EXIST LOCATIONS OF EACH PORTION OF THE SITE TO BE GRANTED ON SITE BY THE SUPERVISING OFFICE.
5. THE CONTRACTED FENCE, EXIST FENCING ALONG THE PERIMETER OF THE SITE, BOUNDARY OR POSSESSION OF THE SITE.
6. REFUSE OR REWARD REQUISITIONED (SCHEDULED) GRANTED FOR ASSESSMENT FOR DETAILS OF TEMPORARY FENCING.
7. EGRESS AND EXGRESS POINTS TO PORTIONS OF SITE PL 10 SHOULD BE VIA POINT X-1-2.

LEGEND:

SITE BOUNDARY

VERDES AREA

SETTING OUT POINT

KORUS AREA PORTBUILT 1 (P1)

KORUS AREA PORTBUILT 2 (P2)

KORUS AREA PORTBUILT 3 (P3)

KORUS AREA PORTBUILT 4 (P4)

KORUS AREA PORTBUILT 5 (P5)

KORUS AREA PORTBUILT 6 (P6)

KORUS AREA PORTBUILT 7 (P7)

KORUS AREA PORTBUILT 8 (P8)

B	TECHER JOSEPH HQ.5	04/07/55	DE
A	TECHER JOSEPH HQ.2	04/07/55	SA
-	TECHER JOSEPH HQ.1	04/07/55	JO
NO BIO	REASON FORES	SA FORES	SA FORES

D DRAINAGE SERVICES DEPARTMENT,
THE GOVERNMENT OF THE MICHIGAN
SPECIAL ADMINISTRATIVE REGION

DETROIT, MICHIGAN 48226-1000 FAX 313 224-2000

WORKS AREA -
PORTIONS P1 TO P8

GRAND: 60041298/C1/10028
圖文書號

[illegible]

WEEK 01	870	13.00
WEEK 02	870	13.00
WEEK 03	870	13.00
WEEK 04	870	13.00
WEEK 05	870	13.00
WEEK 06	870	13.00
WEEK 07	870	13.00
WEEK 08	870	13.00
WEEK 09	870	13.00
WEEK 10	870	13.00
WEEK 11	870	13.00
WEEK 12	870	13.00
WEEK 13	870	13.00
WEEK 14	870	13.00
WEEK 15	870	13.00
WEEK 16	870	13.00
WEEK 17	870	13.00
WEEK 18	870	13.00
WEEK 19	870	13.00
WEEK 20	870	13.00
WEEK 21	870	13.00
WEEK 22	870	13.00
WEEK 23	870	13.00
WEEK 24	870	13.00
WEEK 25	870	13.00
WEEK 26	870	13.00
WEEK 27	870	13.00
WEEK 28	870	13.00
WEEK 29	870	13.00
WEEK 30	870	13.00
WEEK 31	870	13.00
WEEK 32	870	13.00
WEEK 33	870	13.00
WEEK 34	870	13.00
WEEK 35	870	13.00
WEEK 36	870	13.00
WEEK 37	870	13.00
WEEK 38	870	13.00
WEEK 39	870	13.00
WEEK 40	870	13.00
WEEK 41	870	13.00
WEEK 42	870	13.00
WEEK 43	870	13.00
WEEK 44	870	13.00
WEEK 45	870	13.00
WEEK 46	870	13.00
WEEK 47	870	13.00
WEEK 48	870	13.00
WEEK 49	870	13.00
WEEK 50	870	13.00
WEEK 51	870	13.00
WEEK 52	870	13.00
WEEK 53	870	13.00
WEEK 54	870	13.00
WEEK 55	870	13.00
WEEK 56	870	13.00
WEEK 57	870	13.00
WEEK 58	870	13.00
WEEK 59	870	13.00
WEEK 60	870	13.00
WEEK 61	870	13.00
WEEK 62	870	13.00
WEEK 63	870	13.00
WEEK 64	870	13.00
WEEK 65	870	13.00
WEEK 66	870	13.00
WEEK 67	870	13.00
WEEK 68	870	13.00
WEEK 69	870	13.00
WEEK 70	870	13.00
WEEK 71	870	13.00
WEEK 72	870	13.00
WEEK 73	870	13.00
WEEK 74	870	13.00
WEEK 75	870	13.00
WEEK 76	870	13.00
WEEK 77	870	13.00
WEEK 78	870	13.00
WEEK 79	870	13.00
WEEK 80	870	13.00
WEEK 81	870	13.00
WEEK 82	870	13.00
WEEK 83	870	13.00
WEEK 84	870	13.00
WEEK 85	870	13.00
WEEK 86	870	13.00
WEEK 87	870	13.00
WEEK 88	870	13.00
WEEK 89	870	13.00
WEEK 90	870	13.00
WEEK 91	870	13.00
WEEK 92	870	13.00
WEEK 93	870	13.00
WEEK 94	870	13.00
WEEK 95	870	13.00
WEEK 96	870	13.00
WEEK 97	870	13.00
WEEK 98	870	13.00
WEEK 99	870	13.00
WEEK 100	870	13.00

© COPYRIGHT RESERVED



Wetsep treatment tank P8

Project: Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Figure 3 Location Plan for the Wetsep Treatment Tank
