



東業德勤測試顧問有限公司
ETS-TESTCONSULT LTD.

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: eti@ets-testconsult.com
W: www.ets-testconsult.com



ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE

CONTRACT NO. DC/2013/10 - DESIGN,
BUILD AND OPERATE SAN WAI
SEWAGE TREATMENT WORKS –
PHASE 1


**MONTHLY EM&A REPORT
NO. 24**

(01 APRIL – 30 APRIL 2019)

Prepared by:


LO, Ting Yi

Certified by:


LAU, Chi Leung
Environmental Team Leader

Issued Date: 07 May 2019

Report No.: ENA93372

This report shall not be reproduced unless with prior written approval from this laboratory.



Drainage Services Department
Sewage Services Branch
Harbour Area Treatment Scheme
5/F, Western Magistracy
2A Po Fu Lam Road
Hong Kong

Your reference:

Our reference: HKDSD203/50/105736

Date: 9 May 2019

Attention: Mr Albert Wong

BY EMAIL & POST
(email: awong@dsd.gov.hk)

Dear Sirs

Agreement No. HATS 02/2016
Services for Independent Environmental Checker (IEC) for
Contract No. DC/2013/10 – Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Monthly Environmental Monitoring and Audit Report No.24 (April 2019)

We refer to emails of 7 and 8 April 2019 from ETS-Testconsult Limited attaching the Monthly Environmental Monitoring and Audit Report No.24 (April 2019).

We have no further comment and hereby verify the Monthly Environmental Monitoring and Audit Report No.24 (April 2019) in accordance with Clause 5.4 of the Environmental Permit no. EP-464/2013.

Should you have any queries, please do not hesitate to contact the undersigned or our Mr Francis Lau on 2618 2831.

Yours faithfully
ANewR CONSULTING LIMITED

Independent Environmental Checker

LYMA/LHYF/lhmh

cc AECOM – Mr Patrick Leung (email: patrick.leung@swstw-aecom.com)
ETS-Testconsult Limited – Mr C L Lau (email: env@ets-testconsult.com)



TABLE OF CONTENTS

EXECUTIVE SUMMARY

1	INTRODUCTION	1-2
1.1	Basic Project Information	1
1.2	Project Organization	1-2
1.3	Construction Programme	2
1.4	Construction Works Undertaken During the Reporting Period	2
2	AIR QUALITY MONITORING	3-7
2.1	Monitoring Requirements	3
2.2	Monitoring Equipment	3-4
2.3	Monitoring Parameters, Frequency and Duration	4
2.4	Action and Limit Levels	5
2.5	Results and Observations	5
2.6	Event and Action Plan	5-7
3	NOISE MONITORING	8-11
3.1	Monitoring Requirements	8
3.2	Monitoring Equipment	8
3.3	Monitoring Duration and Frequency	8
3.4	Monitoring Locations	8
3.5	Monitoring Methodology	9
3.6	Actions and Limit Level	9
3.7	Results and Observation	9
3.8	Event and Action Plan	10-11
4	WATER QUALITY MONITORING	11-16
4.1	Monitoring Requirements	11
4.2	Monitoring Methodology and Equipment	11
4.3	Monitoring Frequency	12
4.4	Quality Assurance (QA) / Quality Control (QC)	12
4.5	Action and Limit Levels	12-13
4.6	Result and Observation	13
4.7	Event and Action Plan	13-16
5	ENVIRONMENTAL SITE INSPECTION AND AUDIT	16-20
5.1	Site Inspection	16
5.2	Landscape and Visual Audit	17
5.3	Advice on the Solid and Liquid Waste Management Status	17
5.4	Discharge License and Results of Effluent Monitoring	17-18
5.5	Environmental Licenses and Permits	18
5.6	Implementation Status of Environmental Mitigation Measures	18-20
5.7	Summary of Exceedance of the Environmental Quality Performance Limit	20
5.8	Summary of Complaints, Notification of Summons and Successful Prosecution	20
6	FUTURE KEY ISSUES	20-21
6.1	Construction Programme for the Coming Months	20-21
6.2	Key Issues for the Coming Month	21
6.3	Environmental Monitoring and Site Inspection Schedule for the Coming Month	21
7	CONCLUSION	22
7.1	Conclusion	22

LIST OF TABLES

Table 1.1	Contact Information of Key Personnel
Table 2.1	Air Quality Monitoring Equipment
Table 2.2	Monitoring Parameters, Duration and Frequencies of Impact Air Quality Monitoring
Table 2.3	Time Schedule of Impact Air Quality Monitoring
Table 2.4	The criteria of Action and Limit Levels for Air Quality
Table 2.5	Action and Limit Levels for 1-hour TSP and 24-hour TSP
Table 2.6	Event and Action Plan for Air Quality (Dust) during Construction Phase
Table 3.1	Noise Monitoring Equipment
Table 3.2	Time Schedule of Impact Noise Monitoring
Table 3.3	Noise Monitoring Stations
Table 3.4	Action and Limit Levels for Noise Monitoring
Table 3.5	Event/Action Plan for Construction Noise
Table 4.1	Summary of Testing Procedures for water samples
Table 4.2	Monitoring Frequency of Water Quality Monitoring
Table 4.3	Time Schedule of Impact Water Quality Monitoring
Table 4.4	The criteria of Action and Limit Levels for Water Quality
Table 4.5	Action and Limit Levels for Water Quality
Table 4.6	Event and Action Plan for Water Quality
Table 5.1	Summary of Observation of site inspections
Table 5.2	Summary of Quantities of Inert C&D Materials
Table 5.3	Summary of Quantities of C&D Materials
Table 5.4	Summary of Environmental Complaints Notification of Summons and Successful Prosecution

LIST OF APPENDICES

Appendix A	Location of Work Area
Appendix B	Project Organization Chart
Appendix C	Construction Programme
Appendix D1	Calibration Certificates for Impact Air Quality Monitoring Equipment
Appendix D2	Impact Air Quality Monitoring Results
Appendix D3	Graphical Plots of Impact Air Quality Monitoring Results
Appendix E1	Calibration Certificates for Impact Noise Monitoring Equipment
Appendix E2	Impact Noise Monitoring Results
Appendix E3	Graphical Plots of Impact Noise Monitoring Data
Appendix F1	Calibration Certificates for Impact Water Quality Monitoring Equipments
Appendix F2	Impact Water Quality Monitoring Results
Appendix F3	Graphical Plots of Impact Water Quality Monitoring Data
Appendix G	Weather Condition
Appendix H	Environmental Site Inspection Checklists
Appendix I	Landscape and Visual Impact Assessment Checklist
Appendix J	Waste Flow Table
Appendix K	Environmental Licenses and Permits
Appendix L	Implementation Schedule for Environmental Mitigation Measures (EMIS)
Appendix M	Environmental Site Inspection Schedule
Appendix N	Laboratory Report for Discharge Water

FIGURES

Figure 1	Air Quality and Noise Monitoring Stations
Figure 2	Water Quality Monitoring Stations
Figure 3	Location Plan for the Wetsep Treatment Tank



EXECUTIVE SUMMARY

This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Stage 1 (the Project) (hereafter referred to as “the Contract”). The Contract was awarded to ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE (ADCJV) by the Drainage Services Department (DSD) and ETS-Testconsult Limited was appointed as the Environmental Team (ET) by ADCJV to implement the EM&A program in compliance with the EP and the EM&A Manuals.

According to the Section 25 of the Particular Specification (PS) and the Environmental Permit No. EP-464/2013, an EM&A programme should be implemented in accordance with the procedures and requirements in the EM&A Manual of the approved EIA report (Registration No. AEIAR-072/2003). The scope of monitoring works includes air quality, construction noise, water quality and environmental site audit.

Baseline monitoring was completed in April 2017. Action and Limit Levels were established for air quality, noise and water quality parameters based on the baseline monitoring results.

This is the twenty-fourth Monthly Environmental Monitoring and Audit (EM&A) Report for the Contract which summaries findings of the EM&A works conducted during the reporting period from 01 April 2019 to 30 April 2019.

Site Activities

As informed by the Contractor, site activities were carried out in this reporting month:

- *Substructure (rc structure);*
- *Backfilling;*
- *Superstructure (rc and metalworks);*
- *Water Tightness Test;*
- *Internal ABWF – CEPT;*
- *External ABWF – CEPT;*
- *ABWF - UV Disinfection Facility;*
- *ABWF - Sludge Dewatering Building;*
- *ABWF - Administration Building & Maintenance Workshop;*
- *ABWF for the EB1 Transformer Room;*
- *ABWF for the EB2 Transformer Room;*
- *ABWF for the EB3 Transformer Room;*
- *ABWF for the EB4 Transformer Room;*
- *Slope works and Retaining Wall (Eastern Portion);*
- *Slope works and Retaining Wall (Northern Portion);*
- *EVA (Road & Drainage);*
- *RC Trench and Odour Pipe (DO1, DO2);*
- *Emergency By-Pass Pipe;*
- *Sewage Pipe;*
- *Cable Duct and Draw Pits*



Environmental Monitoring and Audit Progress

The monthly EM&A programme was undertaken in accordance with the EM&A Manual for this Contract. The summary of the monitoring activities in this reporting month is listed below:

- 24-hour TSP Monitoring: 6 Occasions at 2 designated locations
- 1-hour TSP Monitoring: 18 Occasions at 2 designated locations
- Noise Monitoring (Day-time): 6 Occasions at 2 designated locations
- Water Quality Monitoring: 13 Occasions at 1 designated location
- Weekly Site inspection: 4 Occasions

Air Quality Monitoring

No exceedance of Action and Limit levels was recorded for 1-hr and 24-hr TSP monitoring in the reporting month.

Noise Monitoring

No exceedance of Action and Limit levels for noise monitoring was recorded in the reporting month.

Water Quality Monitoring

According to the summary of water monitoring results, no exceedance of Action and Limit levels was recorded in this reporting month.

Weekly Site Inspections

In general, performance on environmental mitigation measures implemented was found to be satisfactory in this reporting month. The major findings observed during site inspections are presented in the **Section 5.0**.

Complaint Log

There was no complaint received in relation to the environmental impact during the reporting period.

Notifications of Summons and Successful Prosecutions

There were no notifications of summons or prosecutions received during the reporting period.

Reporting Change

There were no reporting changes during the reporting period.

Future Key Issues

The future key issues to be undertaken in the upcoming month are as follows:

- Chemical and waste management;
- Treatment of runoff and wastewater prior to discharge; and
- Dust and Noise generated from construction activities

1. INTRODUCTION

1.1. Basic Project Information

- 1.1.1. This Monthly Environmental Monitoring and Audit (EM&A) Report is prepared for Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Stage 1 (the Project) (hereafter referred to as “the Contract”). The Contract was awarded to ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE (ADCJV) by the Drainage Services Department (DSD) and ETS-Testconsult Limited was appointed as the Environmental Team (ET) by ADCJV to implement the EM&A program in compliance with the EP and the EM&A Manuals.
- 1.1.2. The project involves expansion of the preliminary treatment works at San Wai STW from 164,000 m³/d to 200,000 m³/d Average Dry Weather Flow, upgrading the preliminary treatment level to CEPT and adding centralized disinfection. The site layout plan is shown in **Appendix A**.
- 1.1.3. According to the Section 25 of the Particular Specification (PS) and the Environmental Permit No. EP-464/2013, an EM&A programme should be implemented by an independent Environmental Team (ET) in accordance with the procedures and requirements in the EM&A Manual of the approved EIA report (Registration No. AEIAR-072/2003). These documents are available through the EIA Ordinance Register. The construction works of the Contract commenced on 16 May 2017.
- 1.1.4. The scope of monitoring works includes air quality, construction noise, water quality and environmental site audit. The EM&A requirements for each parameter described in the following sections include:
- *All monitoring parameters;*
 - *Monitoring schedules for the reporting month and forthcoming months;*
 - *Action and Limit levels for all environmental parameters;*
 - *Event/Action Plans;*
 - *Environmental mitigation measures, as recommended in the Project EIA study final report; and*
 - *Environmental requirements in contract documents.*
- 1.1.5. As part of the project EM&A program, baseline monitoring was conducted from 21 March 2017 to 15 April 2017 to determine the ambient environmental conditions before the project commence any major construction works and it had been verified by IEC and endorsed by EPD.
- 1.1.6. This is the twenty-fourth Monthly Environmental Monitoring and Audit (EM&A) Report for the Contract which summaries the audit findings of the EM&A programme during the reporting period from 01 April 2019 to 30 April 2019.

1.2. Project Organization

- 1.2.1. The project organization structure and lines of communication with respect to the on-site environmental management structure is shown in **Appendix B**. The key personnel contact names and numbers are summarized in **Table 1.1**.

Table 1.1 Contact Information of Key Personnel

Party	Position	Name of Key Staff	Tel. No.	E-mail
Supervising Officer (AECOM Asia Co. Ltd.)	Resident Engineer	Mr. Patrick Leung	5222 6561	patrick.leung@swstw-aecom.com
Independent Environmental Checker (ANewR Consulting Limited)	Technical Director	Mr. Adi Lee	2618 2836	aymlee@anewr.com
Contractor (ATAL-DEGREMONT-CHINA HARBOUR JOINT VENTURE)	Environmental Officer	Mr. Johnny So	9513 8899	johnny.so@c302.checkk.com
Environmental Team (ETS-Testconsult Ltd.)	Environmental Team Leader	Mr. C. L. Lau	2946 7791	env@ets-testconsult.com

1.3. Construction Programme

1.3.1. A copy of the Contractor's construction programme is provided in **Appendix C**.

1.4. Construction Works Undertaken During the Reporting Period

1.4.1. A summary of the construction activities undertaken during this reporting period is shown below:

- *Substructure (rc structure);*
- *Backfilling;*
- *Superstructure (rc and metalworks);*
- *Water Tightness Test;*
- *Internal ABWF – CEPT;*
- *External ABWF – CEPT;*
- *ABWF - UV Disinfection Facility;*
- *ABWF - Sludge Dewatering Building;*
- *ABWF - Administration Building & Maintenance Workshop;*
- *ABWF for the EB1 Transformer Room;*
- *ABWF for the EB2 Transformer Room;*
- *ABWF for the EB3 Transformer Room;*
- *ABWF for the EB4 Transformer Room;*
- *Slope works and Retaining Wall (Eastern Portion);*
- *Slope works and Retaining Wall (Northern Portion);*
- *EVA (Road & Drainage);*
- *RC Trench and Odour Pipe (DO1, DO2);*
- *Emergency By-Pass Pipe;*
- *Sewage Pipe;*
- *Cable Duct and Draw Pits*

2. AIR QUALITY MONITORING

2.1. Monitoring Requirements

- 2.1.1. 1-hr and 24-hr TSP levels were monitored in the reporting month in accordance with the EM&A Manual. Two air monitoring locations were selected which was shown in **Figure 1**.

2.2. Monitoring Equipment

1-hour TSP Monitoring

1-hour TSP levels were measured by using dust meter which are capable of producing comparable results as the by high volume sampling method, to indicate short event impacts. The dust meter is compliant to the clause 1.2.5 of "General Technical Requirement of Environmental Monitoring" and clause 2.2 of "Generic Environmental Monitoring and Audit Manual".

Table 2.1 summarized the dust meter model used during the baseline monitoring. Copies of calibration certificates for dust meters were attached in **Appendix D1**.

Table 2.1 Air Quality Monitoring Equipment

Equipment	Model
Dust Meter	SIBATA LD-3B
High volume sampler (HVS)	Greasby GMW (GS2310)
Calibrator	Tisch TE-5025A

1-hr air quality monitoring (Dust Meter)

Measuring Procedures

The measuring procedures of the dust meter are in accordance with the Manufacturer's instruction Manual as follows:

- Press POWER to ON, check the battery indicator to ensure whether the power supply is enough to conduct the TSP monitoring;
- Press TIMER SET to Manual;
- Press START/STOP SWITCH to start the TSP monitoring;
- Press START/STOP SWITCH to stop the TSP monitoring after monitoring complete;
- Record measured COUNT directly from the dust meter and calculate the TSP level by using the equation of the certificate.

Maintenance & Calibration (QA/QC)

- Dust meter should be checked at 3-month intervals and calibrated at half-year intervals throughout all stages of air quality monitoring.

24-hr air quality monitoring (HVS)

Instrumentation

High volume sampler, as HVS, (Greasby GMWS2310) complete with appropriate sampling inlets were employed for both 1-hour and 24-hour TSP monitoring. The sampler is composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complies with that required by USEPA standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

Installation

The installation of HVS refers to the requirement stated in EM&A Manual.

Operation/Analytical Procedures

Operating/analytical procedures for the operation of HVS are as below:

- Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 0.6m³/min and 1.7m³/min.) in accordance with the manufacturer's

instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50. The flow rate was indicated on the flow rate chart.

- For TSP sampling, fiberglass filters (Whatman G653) were used.
- The power supply was checked to ensure the sampler worked properly.
- On sampling, the sampler was operated 5 minutes to establish thermal equilibrium before placing any filter media at designated air monitoring station.
- The filter holding frame was then removed by loosening the four nuts and carefully a weighted and conditioned filter was centered with the stamped number upwards, on a supporting screen.
- The filter was aligned on the screen so that the gasket formed an air-tight seal on the outer edges of the filter. Then the filter holder frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- The programmable timer will be set for a sampling month of 1 hour or 24 hours. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number.).
- After sampling, the filter was transferred from the filter holder of the HVS to a sealed plastic bag and sent to the laboratory for weighting. The elapsed time was also recoded.
- Before weighting, all filters were equilibrated in desiccators for 24 hour with the temperature of $25^{\circ}\text{C} \pm 3^{\circ}\text{C}$ and the relative humidity (RH) $<50\% \pm 5\%$.

Maintenance & Calibration (QA/QC)

- HVS and their accessories should be maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVS should be calibrated at bi-monthly intervals.

Wind Data Monitoring

Wind data (wind speed and wind direction) were directly extracted from Hong Kong Observatory. All wind data during this reporting month are shown in **Appendix G**.

2.3. Monitoring Parameters, Frequency and Duration

- 2.3.1.** **Table 2.2** summarizes the monitoring parameters, monitoring duration and frequencies of impact air quality monitoring.

Table 2.2 Monitoring Parameters, Duration and Frequencies of Impact Air Quality Monitoring

Parameter	Duration	Frequency
1-hr TSP	1 hr (0800-1900)	Three times per 6 days
24-hr TSP	24 hr	Once per 6 days

- 2.3.2.** In this reporting period, a total of 18 occasions of 1-hour TSP monitoring and 6 events of 24-hour TSP monitoring were undertaken and the schedule was shown in **Table 2.3**

Table 2.3 Time Schedule of Impact Air Quality Monitoring

April 2019						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1	2 ▼	3	4	5	6
7	8 ▼	9	10	11	12	13 ▼
14	15	16	17	18 ▼	19	20
21	22	23	24 ▼	25	26	27
28	29	30 ▼				

Remark: (▼) = Air quality monitoring carried out by ET

2.4. Action and Limit Levels

The criteria for Action and Limit levels have been set out in the contract document of the Project as follows:

Table 2.4 The criteria of Action and Limit Levels for Air Quality

Parameters	Action	Limit
1-hour TSP Level ($\mu\text{g}/\text{m}^3$)	For baseline level $\leq 384\mu\text{g}/\text{m}^3$, Action level = (baseline level plus*1.3 + Limit Level) / 2	500 $\mu\text{g}/\text{m}^3$
	For baseline level $>384\mu\text{g}/\text{m}^3$, Action level = Limit Level	
24-hour TSP Level ($\mu\text{g}/\text{m}^3$)	For baseline level $< 200\mu\text{g}/\text{m}^3$, Action level = (baseline level plus*1.3 + Limit Level) / 2	260 $\mu\text{g}/\text{m}^3$
	For baseline level $\geq 200\mu\text{g}/\text{m}^3$, Action level = Limit Level	

Following the criteria shown in **Table 2.4**, the Action and Limit levels for 1-hour TSP derived as illustrated in **Table 2.5**.

Table 2.5 Action and Limit Levels for 1-hour TSP and 24-hour TSP

Air Quality Monitoring Station	1-hr TSP ($\mu\text{g}/\text{m}^3$)		24-hr TSP ($\mu\text{g}/\text{m}^3$)	
	Action Level	Limit Level	Action Level	Limit Level
ASR1a	309	500	260	260
ASR2b	292	500	228	260

2.5. Results and Observations

2.5.1. 1-hour and 24-hour TSP Monitoring Results

Monitoring data of both 1-hour and 24-hour TSP monitoring carried out in this reporting month are summarized in **Appendix D2**. Graphical presentation of 1-hour and 24-hour TSP monitoring results for the reporting month is shown in **Appendix D3**. Wind data included wind speed and wind direction was extracted from Hong Kong Observatory during this reporting month and is presented in **Appendix G**.

No exceedance of Action and Limit Level of 1-hr TSP and 24-hour TSP monitoring results was recorded during the reporting month.

2.5.2. Observation

Generally, 1-hour TSP and 24-hour TSP monitoring results fluctuated well below the Action Level in this reporting period. The major dust source observed near the monitoring stations was mainly from vehicles passing by the container yards and general earth works. It can be concluded that the contractor implemented sufficient dust mitigation measures during this reporting month.

2.6. Event and Action Plan

If the impact monitoring results exceed the Action and Limit Levels, the actions specified in **Table 2.6** shall be carried out.

Table 2.6 Event and Action Plan for Air Quality (Dust) during Construction Phase

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action Level being exceeded for one sample	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Action Level being exceeded for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC and ER; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency to daily; 5. Discuss with IEC and Contractor on remedial actions required; 6. If exceedance continues, arrange meeting with IEC and ER; 7. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial actions to IEC within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
Limit Level being exceeded for one sample	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IEC, ER and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with Contractor on the possible mitigation measures; 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Check monitoring data and Contractor's working methods; 4. Discuss with 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to ER within 3 working days of notification; 3. Implement the agreed

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
	effectiveness of Contractor's remedial actions; 8. Keep EPD and ER informed of the results.	6. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly.	IEC and Contractor on potential remedial actions; 4. Ensure remedial actions properly implemented.	proposals; 4. Amend proposal if appropriate.
Limit Level being exceeded for two or more consecutive samples	1. Identify source; 2. Inform IEC, ER and EPD the causes & actions taken for the exceedance s; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Investigate the causes of exceedance; 6. Arrange meeting with EPD and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with Contractor on the possible mitigation measures; 3. Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; 4. Supervise the implementation of mitigation measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 4. Discuss with IEC and the Contractor on potential remedial actions; 5. Review Contractor's remedial actions whenever necessary to assure their effectiveness; 6. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to ER within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not resolved; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

3. NOISE MONITORING

3.1. Monitoring Requirements

- 3.1.1. Noise levels (L_{eq} , L_{10} and L_{90}) were monitored in the reporting month in accordance with the EM&A Manual.

3.2. Monitoring Equipment

Sound level meters used for impact noise monitoring were Type 1 sound level meters capable of giving a continuous readout of the noise level reading including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x). They complied with International Electro technical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1). **Table 3.1** summarized the noise monitoring equipment model used during the baseline monitoring. Copies of calibration certificates for noise meters and calibrators were attached in **Appendix E1**.

Table 3.1 Noise Monitoring Equipment

Noise Monitoring Equipment	Model
Sound Level Meter	Rion NL-31 / Rion NL-52
Sound Level Calibrator	Rion NC-73

3.3. Monitoring Duration and Frequency

- 3.3.1. Impact noise monitoring for the A-weighted levels L_{eq} , L_{10} and L_{90} in 30-minute interval was recorded once per 6 days.
- 3.3.2. In this reporting period, a total of 6 occasions of noise monitoring were undertaken and the schedule was shown in **Table 3.2**

Table 3.2 Time Schedule of Impact Noise Monitoring

April 2019						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1	2 ▼	3	4	5	6
7	8 ▼	9	10	11	12	13 ▼
14	15	16	17	18 ▼	19	20
21	22	23	24 ▼	25	26	27
28	29	30 ▼				

Remark: (▼) = Noise monitoring carried out by ET

3.4. Monitoring Locations

Two noise monitoring stations, NSR1a (晉榮貨櫃服務有限公司) and NSR2b (永康貨櫃服務有限公司) which shown in **Figure 1**, were required to perform impact noise monitoring during this reporting period.

The impact noise monitoring programme was summarized in **Table 3.3**.

Table 3.3 Noise Monitoring Stations

Noise monitoring station	Type of Measurement
NSR1a	Façade
NSR2b	Façade

3.5. Monitoring Methodology

Instrumentation

Integrating Sound Level Meters were employed for noise monitoring.

Operation/Analysis Procedures

- The Sound Level Meter was set on a tripod at a height of 1.2m above the ground.
- For free field measurement, the meter was positioned away from any nearby reflective surfaces.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - Frequency weighting : A
 - Time weighting : Fast
 - Time measurement : 30 mins
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1000HZ. If the difference in the calibration level before and after measurement was more than 1 dB(A), the measurement would be considered invalid and repeat measurement would be required after re-calibration or repair of the equipment.
- During the monitoring period, the L_{eq} , L_{10} and L_{90} were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- 3dB(A) correction had been added to the results if noise measurements were free-field.
- Noise monitoring would be cancelled in the presence of fog, rain, storm, wind with a steady speed exceeding 5m/s, or wind gusts exceeding 10m/s.

Maintenance and Calibration (QA/QC)

- The microphone head of the sound level meter and calibrator are cleaned with soft cloth at quarterly intervals.
- The meters are sent to the HOKLAS accredited laboratory or equivalent to check and calibrated at yearly intervals.

3.6. Actions and Limit Level

The Action and Limit Levels were established in **Table 3.4** for noise monitoring.

Table 3.4 Action and Limit Levels for Noise Monitoring

Time Period	Action	Limit
0700 –1900 hrs normal weekdays	When one documented complaint is received	75 dB(A)*

Remark: (*)70dB(A) for schools and 65dB(A) for schools during school examination period

3.7. Results and Observations

3.7.1. Results

Monitoring data of noise monitoring carried out in this reporting month are summarized in **Appendix E2**. Graphical presentation of noise monitoring results for the reporting month is shown in **Appendix E3**.

No exceedance of Action and Limit Level of noise monitoring results was recorded during the reporting month.

3.7.2. Observation

The noise monitoring data were found to be lower than the limit level. The major noise source during the monitoring event was the vehicles passing through the container yard entrance and the general earth works inside the construction site.

3.8. Event and Action Plan

If the impact monitoring results exceed the Action and Limit Levels, the actions specified in **Table 3.5** shall be carried out.

Table 3.5 Event/Action Plan for Construction Noise

EVENT	ACTION			
	ET	IEC	ER	CONTRACTOR
Action level	<ol style="list-style-type: none"> 1. Notify IEC and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IEC and Contractor; 4. Discuss with the Contractor and formulate remedial measures ; 5. Increase monitoring frequency to check the effectiveness of mitigation measures. 	<ol style="list-style-type: none"> 1. Review the analyzed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure mitigation measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposal to IEC; 2. Implement noise mitigation proposals.
Limit level	<ol style="list-style-type: none"> 1. Notify IEC, ER, EPD & Contractor; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, ER and EPD 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analyzed noise problem; 4. Ensure mitigation measures are properly implemented; 5. If exceedances continues, consider what portion of the 	<ol style="list-style-type: none"> 1. Undertake immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of

	<p>the causes and actions taken for the exceedances;</p> <p>7. Assess the effectiveness of Contractor's remedial actions and keep IEC, EPD and ER informed of the results;</p> <p>8. If exceedance stops, cease additional monitoring.</p>		<p>work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</p>	<p>works as determined by ER, until the exceedance is abated.</p>
--	--	--	---	---

4. WATER QUALITY MONITORING

4.1. Monitoring Requirements

- 4.1.1. Water quality was monitored in the reporting month in accordance with the EM&A Manual at one alternative water quality monitoring station, R1b (at Tin Shui Wai Nullah) which shown in **Figure 2**.

4.2. Monitoring Methodology and Equipment

For In-situ Water Quality Measurement

Dissolved Oxygen (DO) measuring equipment

A portable, weatherproof DO-measuring meter with built-in salinity compensation (e.g. YSI 85, YSI Pro 2030 or equivalent) was used in the baseline monitoring. It can be capable for measuring dissolved oxygen level in the range of 0-20 mg/L and 0-200 % saturation.

For Water Sampling and Sample Analysis

Water Sampler

A water sampler comprising a metal bucket was lowered into the water body.

Water Container

The sample container, made by high-density polythene, was rinsed with a portion of the water sample. The water sample was then transferred to the container, labelled with a unique sample ID and sealed with a screw cap. The water samples were stored in a cool box maintained at 4°C. The water samples will then be delivered to Environmental Laboratory of ETS-Testconsult Ltd (HOKLAS Registration No. 022) on the same day for analysis according to the Standard Method APHA 19ed.

The summary of testing methods of testing parameters required was shown in **Table 4.1**.

Table 4.1 Summary of Testing Procedures for water samples

Parameters	Testing Procedure	Detection Limit
Turbidity	Dissolved Oxygen Meter Measurement	0.1 NTU
Dissolved Oxygen	In house method refer to APHA 19 th ed 2130 B	0.01 mg/L
Total suspended solids	In house method refer to APHA 19 th ed 2540D	0.1 mg/L

4.3. Monitoring Frequency

- 4.3.1. Water samples were collected 3 times per week in 1 monitoring station. Three parameters including turbidity, dissolved oxygen and total suspended solids would be tested.

Table 4.2 Monitoring Frequency of Water Quality Monitoring

Parameters	Frequency	No. of sampling stations
Turbidity	3 times per week	1 station
Dissolved Oxygen		
Total suspended solids		

- 4.3.2. In this reporting period, a total of 13 occasions of water quality monitoring were undertaken and the schedule was shown in **Table 4.3**

Table 4.3 Time Schedule of Impact Water Quality Monitoring

April 2019						
Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
	1	2 ▼	3	4 ▼	5	6 ▼
7	8	9 ▼	10	11 ▼	12	13 ▼
14	15	16 ▼	17	18 ▼	19	20 ▼
21	22	23 ▼	24	25 ▼	26	27 ▼
28	29	30 ▼				

Remark: (▼) = Water quality monitoring carried out by ET

4.4. Quality Assurance (QA) / Quality Control (QC)

For in-situ measurements, at each measurement / sampling, two consecutive measurements of turbidity and dissolved oxygen (DO) were taken. The probes were retrieved out of the water after the first measurement and then re-deployed for the second measurement. If the difference between the first and second measurement is greater than 25% the reading will be discarded and the measurements will be repeated.

For laboratory analysis of water, test method of all test parameters and the QA/QC samples were carried out in accordance with the requirements of HOKLAS.

For our QA/QC procedure, one QC sample, one duplicate sample and one sample spike of every batch of 20 samples were analyzed.

The calibration certifications of water quality monitoring equipments were shown in **Appendix F1**.

4.5. Actions and Limit Levels

The criteria for Action and Limit Levels have been set out as follows:

Table 4.4 The criteria of Action and Limit Levels for Water Quality

Parameters	Unit	Action Level	Limit Level
Turbidity	NTU	95%ile of baseline data	99%ile of baseline data
Dissolved Oxygen	mg/L	5%ile of baseline data	1%ile of baseline data
Suspended solids	mg/L	95%ile of baseline data	99%ile of baseline data

Following the criteria shown in **Table 4.4**, the Action and Limit Levels for monitoring parameters derived as illustrated in **Table 4.5**.

Table 4.5 Action and Limit Levels for Water Quality

Parameters	Unit	Action	Limit
Turbidity	NTU	19.8	20.5
Dissolved Oxygen	mg/L	1.84	1.81
Suspended Solid	mg/L	17.0	17.8

4.6. Result and Observation

4.6.1. Result

Monitoring data of water quality monitoring carried out in this reporting month are summarized in **Appendix F2**. Graphical presentation of the monitoring results for the reporting month is shown in **Appendix F3**.

No exceedance of Action and Limit Level of water quality monitoring results was recorded during the reporting month.

4.6.2. Observation

Generally, the turbidity and suspended solids were found to be lower than the action level. Besides, all results of dissolved oxygen measured in this reporting month were higher than the action level.

4.7. Event and Action Plan

If the impact monitoring results of the individual parameters exceed the Action and Limit Levels, the actions specified in **Table 4.6** shall be carried out.

Table 4.6 Event and Action Plan for Water Quality

Event	Action			
	ET Leader	IEC	ER	Contractor
Action Level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC and Contractor; 6. Repeat 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IEC on the proposed mitigation measures; 2. make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment 4. Consider changes of working methods; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER; 6. Implement the agreed mitigation measures.



Event	Action			
	ET Leader	IEC	ER	Contractor
	measurement on next day of exceedance.			
Action Level being exceeded by more than two consecutive sampling days	<ol style="list-style-type: none"> 1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC and Contractor; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC and Contractor; 6. Ensure mitigation measures are implemented; 7. Prepare to increase the monitoring frequency to daily; 8. Repeat measurement on next day of exceedance. 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Discuss with IEC on the proposed mitigation measures; 2. Make agreement on the mitigation measures to be implemented; 3. Assess the effectiveness of the implemented mitigation measures. 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET and IEC and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures.
Limit Level being exceeded by one sampling day	<ol style="list-style-type: none"> 1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC, Contractor 	<ol style="list-style-type: none"> 1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise 	<ol style="list-style-type: none"> 1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 	<ol style="list-style-type: none"> 1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment;



Event	Action			
	ET Leader	IEC	ER	Contractor
	4. or and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are implemented; 7. Increase the monitoring frequency to daily until no exceedance of Limit Level.	3. the ER accordingly; Assess the effectiveness of the implemented mitigation measures.	3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures.	4. Consider changes of working methods; 5. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures.
Limit Level being exceeded by more than two consecutive sampling days	1. Repeat in-situ measurement to confirm findings; 2. Identify reasons for non-compliance and sources of impact; 3. Inform IEC, Contractor and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, ER and Contractor; 6. Ensure mitigation measures are	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures.	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Assess the effectiveness of the implemented mitigation measures; 5. Consider and instruct, if necessary, the Contractor to slow down or	1. Inform the ER and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment; 4. Consider changes of working methods; 5. Discuss with ET, IEC and ER and propose mitigation measures to IEC and ER within 3 working days; 6. Implement the agreed mitigation measures; 7. As directed by

Event	Action			
	ET Leader	IEC	ER	Contractor
	7. implemented; Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days.		to stop all or part of the marine work until no exceedance of Limit Level.	the ER, to slow down or to stop all or part of the marine work or construction activities.

5. ENVIRONMENTAL SITE INSPECTION AND AUDIT

5.1. Site Inspection

- 5.1.1. Site Inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control mitigation measures for the project. During the reporting period, site inspections were carried out on 04, 12, 18 & 26 April 2019.
- 5.1.2. Observations for the site inspections within this reporting period are summarized in **Table 5.1** and inspection checklists are attached in **Appendix H**.

Table 5.1 Summary of observation of site inspections

Date	Observations/ Reminders	Follow-up Action	Closed Date
28 March 2019	1. Oil container was observed without drip tray. 2. C&D waste and general refuse was observed stored together.	1. The chemical container was removed. 2. The general refuse and C&D wastes were collected.	04 April 2019
04 April 2019	1. General refuse was observed.	1. The general refuse were collected.	12 April 2019
12 April 2019	--	--	--
18 April 2019	1. Fill material was found without cover at UV Zone. 2. Stagnant water was observed at SDB Zone.	1. Fill material was covered properly at UV Zone. 2. Stagnant water was cleared.	26 April 2019
26 April 2019	1. Stagnant water was accumulated on the drip tray at P1 Zone.	Follow-up actions for outstanding observation will be inspected during the next site inspection.	--

5.2. Landscape and Visual Audit

- 5.2.1. Landscape and visual audits were undertaken at least once every two weeks throughout the construction period by a competent landscape architect. During the reporting period, audits were carried out on 04 and 19 April 2019.
- 5.2.2. Observations and reminders were summarized in the landscape and visual impact assessment checklists which are attached in **Appendix I**.

5.3. Advice on the Solid and Liquid Waste Management Status

- 5.3.1. All types of waste arising from the construction work are classified into the following:
- Construction & Demolition (C&D) Material;
 - Chemical Waste;
 - General Refuse; and
 - Excavated Soil
- 5.3.2. The quantities of waste for disposal in this Reporting Period are summarized in **Table 5.2** and **Table 5.3** and the Monthly Summary Waste Flow Table is shown in **Appendix J**. Whenever possible, materials were reused on-site as far as practicable.

Table 5.2 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
Reused in this Contract (Inert) (m ³)	0	--
Reused in other Projects (Inert) (m ³)	0	--
Disposed as Public Fill (Inert) (m ³)	625	Tuen Mun 38 Fill Bank

Table 5.3 Summary of Quantities of C&D Materials

Type of Waste	Quantity	Disposal Location
Recycled Metal (kg)	0	--
Recycled Paper / Cardboard Packing (kg)	200	--
Recycled Plastic (kg)	0	--
Chemical Wastes (kg)	0	--
General Refuses (m ³)	129,800	North East New Territories (NENT) Landfill

- 5.3.3. To control over the site performance on waste management, the Contractor shall ensure that all solid and liquid waste management works are in full compliance with the relevant license/permit requirements, such as the effluent discharge license and the chemical waste producer registration. The Contractor is also reminded to implement the recommended environmental mitigation measures according to the EM&A Manual based on actual site conditions.

5.4. Discharge License and Results of Effluent Monitoring

- 5.4.1. Effluent quality was monitored in the reporting month in accordance with the EM&A Manual at the discharge point. A discharge license under Water Pollution Control Ordinance was obtained by the Contractor upon commencement of the Project. Self-monitoring would be performed as per the requirement under the discharge license. According to the EM&A Manual, pH, chemical oxygen demand and total suspended solid are required to be analysed at least once every two week.
- 5.4.2. Effluent water samples were scheduled to be collected on 09 and 23 April 2019. As only Wetsep at P1a was operated on April 2019, the effluent water sample was sampled at P1a only on the reporting month. The required testing parameter including pH, chemical oxygen demand and total suspended solid were carried out in a HOKLAS laboratory. The methods of chemical oxygen demand and total

suspended solid determination follow APHA 19ed 5220 B and APHA 19ed 2540 D respectively. The laboratory reports for the discharge water are presented in **Appendix N**.

- 5.4.3. For effluent quality monitoring as per the discharge license requirement, the results complied with the discharge license requirement.

5.5. Environmental Licenses and Permits

- 5.5.1. The valid environmental licenses and permits during the reporting period are summarized in **Appendix K**.

5.6. Implementation Status of Environmental Mitigation Measures

- 5.6.1. The environmental mitigation measures that recommended in the Environmental Monitoring and Audit Manual covered the issues of dust, noise, water and waste and they are summarized as following:

Dust Mitigation Measures

- a. The working area for the uprooting of trees, shrubs, or vegetation or for the removal of boulders, poles, pillars or temporary or permanent structures should be sprayed with water or a dust suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;
- b. All demolished items (including trees, shrubs, vegetation, boulders, poles, pillars, structures, debris, rubbish and other items arising from site clearance) that may dislodge dust particles should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition;
- c. Vehicle washing facilities including a high pressure water jet should be provided at every discernible or designated vehicle exit point;
- d. The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;
- e. Where a site boundary adjoins a road, street, service and or other area accessible to the public, hoarding of not less than 2.4m from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit;
- f. Every main haul road (i.e. any course inside a construction site having a vehicle passing rate of higher than 4 in any 30 minutes) should be paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical so as to maintain the entire road surface wet;
- g. The portion of any road leading only to a construction site that is within 30m of a discernible or designated vehicle entrance or exit should be kept clear of dusty materials;
- h. Immediately before leaving a construction site, every vehicle should be washed to remove any dusty materials from its body and wheels;
- i. Where a vehicle leaving a construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle;
- j. The working area of any excavation or earth moving operation should be sprayed with water or a dusty suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;
- k. Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabilizer within 6 months after the last construction activity on the construction site or part of the construction site where the exposed earth lies;
- l. Any stockpile of dusty material should be either covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or a dust suppression chemical so as to maintain the entire surface wet.

Noise Mitigation Measures

- a. Quiet plants should be used in order to reduce the noise impacts to protect the nearby NSRs.
- b. Temporary and Movable Noise Barriers should be used in order to reduce the noise impact to the surrounding sensitive receivers
- c. The contractor should site noisy equipment and activities as far from sensitive receivers as practical.
- d. Idle equipment should be turned off or throttled down.
- e. Construction activities should be planned so that parallel operation of several sets of equipment close to a given receiver is avoided
- f. Construction plant should be properly maintained and operated.

Water Quality Mitigation Measures

- a. Exposed stockpiles should be covered with tarpaulin or impervious sheets before a rainstorm occurs;
- b. The exposed soil surfaces should also be properly protected to minimize dust emission;
- c. The stockpiles of materials should be placed in the locations away from the drainage channel so as to avoid releasing materials into the channel;
- d. Wheel washing facilities should be provided at site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles;
- e. Provision of site drainage systems and treatment facilities would be required to minimize the water pollution;
- f. A discharge license needs to be applied from EPD for discharging effluent from the construction site;
- g. The treated effluent quality is required to meet the requirements specified in the discharge license;
- h. Provision of chemical toilets is required to collect sewage from workforce. The chemical toilets should be cleaned on a regular basis;
- i. A licensed waste collector should be employed to clean the chemical toilets and temporary storage tank on a regular basis;
- j. Illegal disposal of chemicals should be strictly prohibited;
- k. Registration as a chemical waste producer is required if chemical wastes are generated and need to be disposed of. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes;
- l. Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance should be used as a guideline for handling chemical wastes;
- m. The impact from accidental spillage of chemicals can be effectively controlled through good management practices.

Waste Management Mitigation Measures

- a. Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;
- b. To encourage collection of aluminium cans by individual collectors, separate bins should be provided to segregate this waste from other general refuse generated by the workforce;
- c. Any unused chemicals or those with remaining functional capacity should be recycled;
- d. Prior to disposal of C&D waste, it is recommended that wood, steel and other metals be separated for re-use and/or recycling and inert waste as fill material to minimize the quantity of waste to be disposed of to landfill;
- e. Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and
- f. Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.

5.6.2. An updated summary of the Environmental Mitigation Implementation Schedule (EMIS) is presented in **Appendix L**. Most of the necessary mitigation measures were implemented properly. Any deficiencies were noted in the remarks of the schedule.

5.7. Summary of Exceedance of the Environmental Quality Performance Limit

5.7.1. There was no Action and Limit level exceedance of 1-hour and 24-hr TSP monitoring was recorded at station ASR1a and ASR2b during this reporting month.

5.7.2. There was no Action and Limit Level exceedance for noise recorded at station NSR1a and NSR2b during the reporting period.

5.7.3. There was no Action and Limit Level exceedance for water quality monitoring recorded at station R1b during the reporting period.

5.8. Summary of Complaints, Notification of Summons and Successful Prosecution

5.8.1. There were no complaints received during the reporting period.

5.8.2. There were no notifications of summons or prosecutions received during the reporting period.

5.8.3. A summary of environmental complaints, notifications of summons and successful prosecutions was given in **Table 5.4**.

Table 5.4 Summary of Environmental Complaints Notification of Summons and Successful Prosecution

Reporting Period	Cumulative Statistic		
	Complaints	Notifications of summons	Successful prosecutions
The reporting period	0	0	0
From commencement date of construction to end of reporting month	0	0	0

6. FUTURE KEY ISSUES

6.1. Construction Programme for the Coming Months

6.1.1. As informed by the Contractor, the major construction activities for May 2019 are included:

- Substructure (rc structure);
- Backfilling;
- Superstructure (rc and metalworks);
- Water Tightness Test;
- Internal ABWF – CEPT;
- Substructure (ELS & Bulk excavation);
- Removal of ELS;
- ABWF – UV Disinfection Facility, Sludge Dewatering Building, Administration Building & Maintenance Workshop, Electrical Building No.1, Electrical Building No.2, Electrical Building No.3, Electrical Building No.4, Payment Flowmeter Chamber;
- Site Formation along Boundary Wall (Perimeter);
- Slope works and Retaining Wall (Eastern Portion);
- Slope works and Retaining Wall (Northern Portion);

- Drainage Outlet connection to the Existing Stormwater Drainage System along Ha Tsuen Road;
- CLP Cable Duct and Draw Pits (within the Site);
- EVA (Road & Drainage);
- RC Trench and Odour Pipe (DO1, DO2);
- Process Pipe;
- Emergency By-Pass Pipe;
- Sewage Pipe;
- Cable Duct and Draw Pits;
- WSD External Watermain Laying Works;
- Internal Watermain Laying Works

6.2. Key Issues for the Coming Month

Key issues to be considered in the coming month include:

- Chemical and waste management;
- Treatment of runoff and wastewater prior to discharge; and
- Dust and Noise generated from construction activities;

Mitigation measures to be required in the coming month:

Air Quality Impact

- To provide adequate water spraying in the worksite;
- To operate and maintain automatic wheel washing facilities properly;
- To provide road sweeping site entrance and public roads outside site entrance;
- To ensure implementation of the dust mitigation measures for the site activities;
- To maintain proper operation of the mist spraying system;
- To provide proper maintenance for vehicles and machines on site; and
- To investigate any other dust sources around the air sensitive receivers

Noise

- To switch off equipment if not in use;
- To operate silent equipment;
- To identify the noise sources inside and outside of the site; and
- To follow up any exceedance caused by the construction work inside the worksite

Water Quality Impact

- To ensure the drainage system was maintained properly;
- To maintain the existing silt trap to ensure good efficiency of wheel wash facilities;
- To avoid stagnant water in the drip trays due to rainfall;
- To avoid any stagnant water or provide insecticide to avoid mosquito breeding

Chemical and Waste Management

- To remove waste from the site regularly;
- To properly store and handle chemical wastes on site;
- To implement trip ticket system for all the imported public fill and general refuse disposal;
- To maintain proper housekeeping;
- To identify C&D material by packaging, labelling, storage, transportation and disposal in accordance with statutory regulations.

6.3. Environmental Monitoring and Site Inspection Schedule for the Coming Month

- 6.3.1. The tentative schedule for environmental monitoring and site inspection schedule for May 2019 is provided in **Appendix M**.



7. CONCLUSION


7.1. Conclusions

- 7.1.1.** There was no Action and Limit level exceedance of 1-hour and 24-hr TSP monitoring was recorded at station ASR1a and ASR2b during this reporting month.
- 7.1.2.** There was no Action and Limit Level exceedance for noise recorded at station NSR1a and NSR2b during the reporting period.
- 7.1.3.** There was no Action and Limit Level exceedance for water quality monitoring recorded at station R1b during the reporting period.
- 7.1.4.** There were no complaints received during the reporting period.
- 7.1.5.** There were no notifications of summons or prosecutions received during the reporting period.

- END OF REPORT -


Appendix A

Location of Works Areas

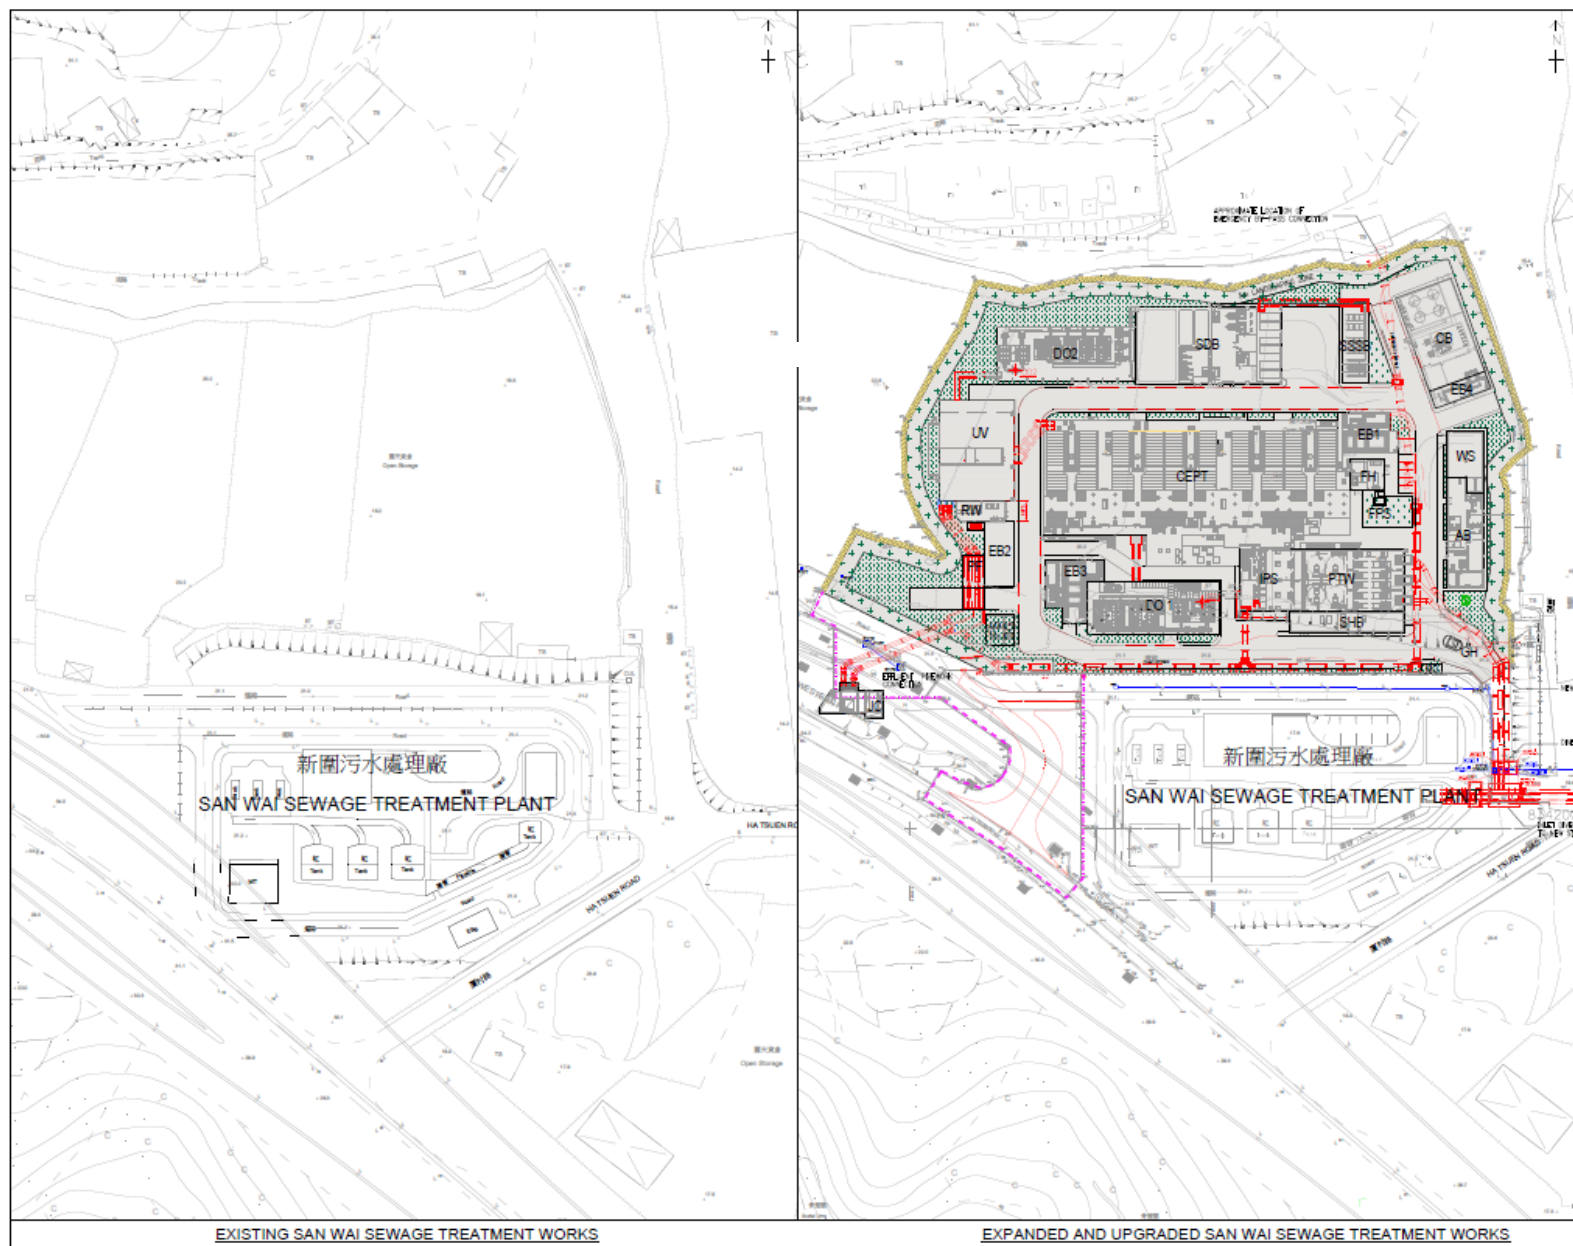

Appendix B

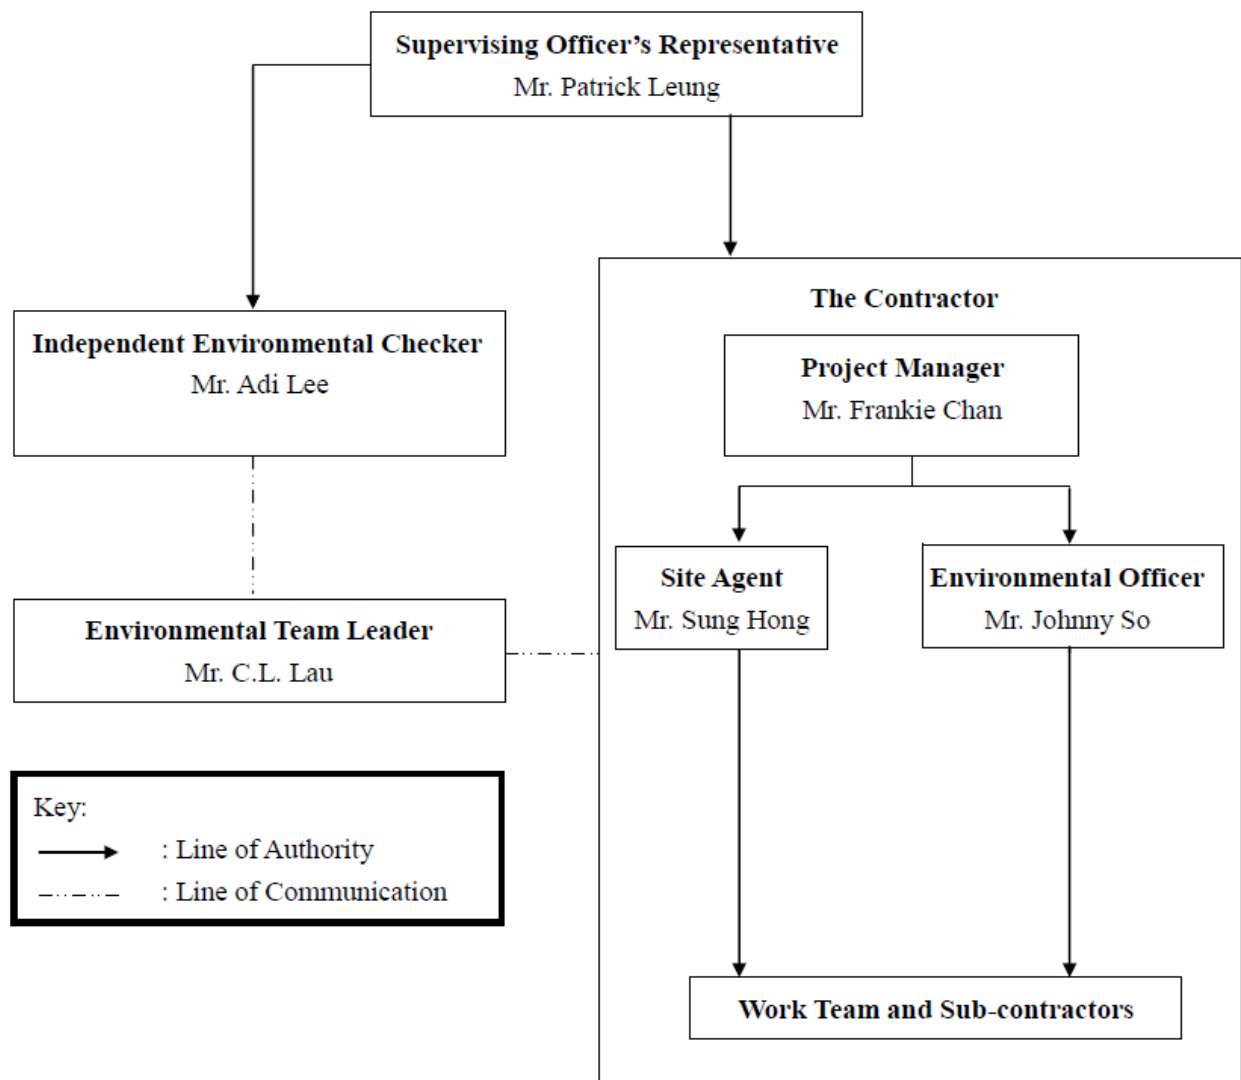


Project Organization Chart



Appendix C

Construction Programme

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 1 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
San Wai Sewage Treatment Works Phase 1 - Rev 10 MP (Update as of 30 Apr 2019)			1672	27-May-16 A	23-Dec-20				
Key Date			1672	27-May-16 A	23-Dec-20				
Commencement & Completion of Works			1672	27-May-16 A	23-Dec-20				
KD150	Section 1 - Handover to Home Affairs Department for Maintenance	1120	30-Nov-17 A	23-Dec-20					
KD160	Section 2 - Period of Works (FOT P.3 of 67, 71) - Including 88.5 Days Granted EOT	1672	27-May-16 A	23-Dec-20					
Plant Room Handover Dates To E&M Installation			89	03-May-19	30-Jul-19				
KD302	Inlet Works, Preliminary Treatment Units & Inlet Pumping Station (PTW & IPS)	0		20-Jun-19					
KD304	Solid Handling Building (SHB)	0		14-Jul-19					
KD306	System Control Flowmeter Chamber (SF)	0		01-Jul-19					
KD308	Chemically Enhanced Primary Treatment (CEPT)	0		15-Jul-19					
KD310	Deodorization Facilities No.1 (DO 1)	0		15-Jul-19					
KD312	Deodorization Facilities No.2 (DO 2)	0		30-Jul-19					
KD316	UV Disinfection Facilities (UV)	0		15-Jun-19					
KD318	Re-use Water Building (RW)	0		27-Jun-19					
KD320	Payment Flowmeter Chamber (PF)	0		22-Jun-19					
KD324	Chemical Building (CB)	0		22-Jun-19					
KD326	Electrical Building No.1 (EB1)	0		03-May-19					
KD336	Street Fire Hydrant Pump Room & GENSET Room (FH)	0		30-Jun-19					
KD341	Foul Water Pump Sump (FW)	0		30-Jun-19					
Preliminaries & General Requirement			1362	01-Apr-17 A	22-Dec-20				
Contractor Requirement			1362	01-Apr-17 A	22-Dec-20				
PS465	Impact Monitoring	1275	27-Jun-17 A	22-Dec-20					
PS485	Site Drainage Plan Implementation	1362	01-Apr-17 A	22-Dec-20					
Design & Design Checking of Permanent Works			1639	26-Jun-16 A	21-Dec-20				
Statutory Submission			1377	15-Mar-17 A	21-Dec-20				
DS150	Application of Discharge License for Operation	180	07-May-19	03-Nov-19					
DS166	CLP - Photovoltaic Panel Connection	496	24-Dec-17 A	03-May-19					
DS173	PCCW - Telephone Lines and Megalink	678	27-Jun-17 A	06-May-19					
DS174	PCCW - Telephone Lines for CLP Summation Metering	645	28-Jul-17 A	03-May-19					
DS177	EMSD - Passenger Lift	340	29-May-18 A	03-May-19					
DS180	EPO - Application for Emergency Generator Flue Gas Discharge License	180	28-Nov-18 A	26-May-19					
DS195	BEAM Plus - Final Assessment (FA)	1026	01-Mar-18 A	21-Dec-20					
DS200	ArchSD - VCAB and DAP Submission and Approval	784	15-Mar-17 A	07-May-19					
AIP / DDA Submission & Approval			1119	26-Jun-16 A	20-Jul-19				
DS410	Review & Revisions of Design Plan	1049	26-Jun-16 A	10-May-19					
Design Memorandum (AIP1 / DDA1)			433	13-May-18 A	20-Jul-19				
DS505	DDA1 - Design Memorandum - Design Preparation to SO Approval	433	13-May-18 A	20-Jul-19					
Global Design			916	06-Jan-17 A	10-Jul-19				
Electrical Power Supply System (AIP20 / DDA20ABCE)			777	24-Apr-17 A	09-Jun-19				
DG1891	DDA20A - Electrical Power Supply System - Design Preparation to SO Approval	777	24-Apr-17 A	09-Jun-19					

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining Work
 Milestone



TASK filter: 3 Months Rolling Programme.

CONTRACT NO. DC/2013/10 DESIGN, BUILD & OPERATE
SAN WAI SEWAGE TREATMENT WORKS - PHASE 1
MASTER PROGRAMME Rev 10 (30 April 2019)
THREE (3) MONTHS ROLLING PROGRAMME

Date	Revision	Checked	Approved
30-Apr-19	Three (3) Months Rolling Programme...		

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 2 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
Control and Monitoring System (AIP21 / DDA21ABCEDE)									
DG1924	DDA21A - Process & Instrumentation Diagram (P&ID) - Design Preparation to SO Approval	910	12-Jan-17 A	10-Jun-19					
DG1940	DDA21B - System Control Philosophy - Design Preparation to SO Approval	879	12-Jan-17 A	09-Jun-19					
DG1956	DDA21C - Functional Design Specification - Design Preparation to SO Approval	817	20-Mar-17 A	14-Jun-19					
DG1972	DDA21D - PLC, SCADA & I/O Allocation Schedules - Design Preparation to SO Approval	785	03-Apr-17 A	28-May-19					
DG1988	DDA21E - SCADA Graphic Interface - Design Preparation to SO Approval	765	23-Apr-17 A	28-May-19					
DG1988	DDA21E - SCADA Graphic Interface - Design Preparation to SO Approval	740	01-Jul-17 A	10-Jun-19					
Landscaping Works (AIP22 / DDA22AB)									
DG1260	DDA22A - Landscaping Works (Green Roof) - Design Preparation to SO Approval	889	06-Jan-17 A	13-Jun-19					
DG1274	DDA22B - Landscaping Works (Site Wide) - Design Preparation to SO Approval	850	06-Jan-17 A	05-May-19					
DG1274	DDA22B - Landscaping Works (Site Wide) - Design Preparation to SO Approval	711	03-Jul-17 A	13-Jun-19					
Testing and Commissioning Plan (AIP23 / DDA23)									
DG3305	DDA23 - Detailed Testing & Commissioning Plan - Design Preparation to SO Approval	416	22-Apr-18 A	12-Jun-19					
General Notes Drawings for Foundation and Civil & Structural (AIP24AB / DDA24AB)									
General Notes Drawings for Civil & Structural (AIP24B / DDA24BC)									
DG3706	DDA24C - Typical Details for Architecture - Design Preparation to SO Approval	803	22-Feb-17 A	05-May-19					
DG3706	DDA24C - Typical Details for Architecture - Design Preparation to SO Approval	803	22-Feb-17 A	05-May-19					
Site Formation (AIP26 / DDA26)									
DG660	DDA26 - Site Formation - Design Preparation to SO Approval	864	14-Jan-17 A	28-May-19					
Sewerage and Drainage Works (AIP27B / DDA27BC1C2DEF)									
Civil and Structural Design (AIP27B / DDA27BD)									
DG960	DDA27B - Sewerage and Drainage Works - Design Preparation to SO Approval	834	21-Feb-17 A	05-Jun-19					
DG960	DDA27B - Sewerage and Drainage Works - Design Preparation to SO Approval	812	21-Feb-17 A	13-May-19					
DG988	DDA27D - Detailed Design Report for Pipe Trenches - C&S - Design Preparation to SO Approval	758	08-May-17 A	05-Jun-19					
Boundary Wall & Entrance (AIP28 / DDA28AB)									
DG1160	DDA28A - Slopes and Retaining Wall - Design Preparation to SO Approval	872	03-Feb-17 A	24-Jun-19					
DG1160	DDA28A - Slopes and Retaining Wall - Design Preparation to SO Approval	819	03-Feb-17 A	02-May-19					
DG1195	DDA28B - Boundary Wall & Entrance - Design Preparation to SO Approval	738	17-Jun-17 A	24-Jun-19					
Site Wide Utility (AIP30 / DDA30ABCEFGI)									
DG3515	DDA30A - Site Wide Security Access Control & Communication System - Design Preparation to SO Approval	877	30-Jan-17 A	25-Jun-19					
DG3515	DDA30A - Site Wide Security Access Control & Communication System - Design Preparation to SO Approval	863	30-Jan-17 A	11-Jun-19					
DG3816	DDA30E - Site Wide Utility (Road Lighting) - Design Preparation to SO Approval	719	23-Jun-17 A	11-Jun-19					
DG3830	DDA30F - Typical Electrical Installation Drawings - Design Preparation to SO Approval	748	08-Jun-17 A	25-Jun-19					
DG3844	DDA30G - Typical Building Services Installation Drawings - Design Preparation to SO Approval	721	23-Jun-17 A	13-Jun-19					
HAZOP Report (DDA31B)									
DG3545	DDA31B - Hazardous Zoning Classification Report - Design Preparation to SO Approval	609	01-Sep-17 A	02-May-19					
ELS / Bulk Excavation (Temporary Works)									
ELS for Inlet Pipe Connection									
DG3755	ELS for Inlet Pipe Connection - Design Preparation to DC and SO Approval	603	04-Sep-17 A	30-Apr-19					
Miscellaneous Design									
Equipment Schedules (DDA32A)									
DG2012	DDA32A - Equipment Schedules - Design Preparation to SO Approval	673	03-Jul-17 A	06-May-19					
Instrumentation Schedules (DDA32F)									
DG3234	DDA32F - Instrumentation Schedules - Design Preparation to SO Approval	673	03-Jul-17 A	06-May-19					
LOT #1 - Building / Facilities Design : CEPT+SF, PTW+IPS+SHB, UV, SDB+SSSB									
Inlet Work, Preliminary Treatment Works, IPS and SHB									
Electrical and Mechanical Design (AIP5B / DDA5C1C2DEF)									
DB1264	DDA5C1-2 - PTW, IPS & SHB - (Super Structural Design) - GA Drawing - Design Preparation to SO Approval	784	01-Apr-17 A	25-May-19					
UV Disinfection Facilities									
Electrical and Mechanical Design (AIP7B / DDA7C1C2DEF)									
DB1352	DDA7C1-1 - UV Facilities - (Piling & Foundation Design) - GA Drawing - Design Preparation to SO Approval	881	22-Dec-16 A	22-May-19					
Sludge Dewatering Building and Sludge Skip Storage Building									
		759	29-Apr-17 A	27-May-19					

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 3 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
Electrical and Mechanical Design (AIP9B / DDA8C1C2DEF)									
DB1476	DDA8C1-2 - SDB and SSSB - (Super Structural Design) - GA Drawing - Design Preparation to SO Approval	759	29-Apr-17 A	27-May-19					
LOT #2 - Building / Facilities Design : AB+WS, DO, CB+EB4, FH									
Administration Building & Maintenance Workshop									
Electrical and Mechanical Design (AIP10B / DDA10C1C2DEF)									
DB2286	DDA10C1-1 - Admin Bldg. & Workshop (Piling & Foundation Design) - GA Drawing - Design Preparation to SO Approval	964	03-Oct-16 A	25-May-19					
Deodorization Facilities No.1 and No.2									
Electrical and Mechanical Design (AIP9B / DDA9C1C2DEF)									
DB2348	DDA9C1 - DO #1 & #2 - GA Drawing - Design Preparation to SO Approval	866	15-Dec-16 A	30-Apr-19					
Street Fire Hydrant Pump Room & GENSET Room									
Electrical and Mechanical Design (AIP17B / DDA17C1C2DE)									
DB2448	DDA17C1 - FH Pump Room & GENSET Room - GA Drawing - Design Preparation to SO Approval	915	07-Dec-16 A	09-Jun-19					
DB4648	DDA17D - FH Pump Room & GENSET Room - Electrical - Design Preparation to SO Approval	811	23-Mar-17 A	12-Jun-19					
LOT #3 - Building / Facilities Design : EB1, EB2, EB3, EB4, RW, DG+ICW, Inlet/Outlet Connection									
Electrical Building No.1, No.2, No.3, No.4									
Electrical and Mechanical Design for EB1234 (AIP13B / DDA13C1C2DE)									
DB3148	DDA13C1 - EB1, EB2, EB3 & EB4 - GA Drawing - Design Preparation to SO Approval	1004	16-Sep-16 A	16-Jun-19					
ICW and DG Store & Chemical Waste Storage Building									
Civil and Structural Design (AIP16A / DDA16AB)									
DB3323	DDA16A - ICW, DG & Chemical Stores - C&S - Design Preparation to SO Approval	567	16-Oct-17 A	05-May-19					
Electrical and Mechanical Design (AIP16B / DDA16C1C2D)									
DB3348	DDA16C1 - ICW, DG & Chemical Stores - GA Drawing - Design Preparation to SO Approval	925	30-Nov-16 A	13-Jun-19					
DB4694	DDA16D - ICW, DG & Chemical Stores - Building Services - Design Preparation to SO Approval	749	24-May-17 A	12-Jun-19					
LOT #4 - Building / Facilities Design : GH, PF									
Gatehouse									
Civil and Structural Design (AIP18A / DDA18AB)									
DB4434	DDA18A - Gatehouse - C&S - Design Preparation to SO Approval	654	18-Jul-17 A	02-May-19					
Electrical and Mechanical Design (AIP18B / DDA18C)									
DB4754	DDA18C - Gatehouse - Building Services - Design Preparation to SO Approval	775	24-Apr-17 A	08-Jun-19					
Civil & Structural Works									
LOT #1 - Bldg / Facilities Const. (Arch'l & Struct'l) : CEPT+SF, PTW+IPS+SHB, UV, SDB+SSSB									
Chemically Enhanced Primary Treatment (CEPT)									
CS1526	Backfilling (except in Water Tightness Test area)	375	28-Apr-18 A	08-May-19					
CS1530	Superstructure (rc and metalworks)	509	22-Feb-18 A	15-Jul-19					
CS1534	Water Tightness Test - Backfilling	87	11-Mar-19 A	05-Jun-19					
CS1540	Internal ABWF - CEPT	127	11-Mar-19 A	15-Jul-19					
System Control Flowmeter Chamber (SF)									
CS1400	Substructure (rc structure)	26	20-May-19	14-Jun-19					
CS1405	Backfilling	2	13-Jun-19	14-Jun-19					
CS1410	Superstructure (rc and metalworks)	12	13-Jun-19	24-Jun-19					
CS1420	ABWF - System Control Flowmeter Chamber	7	25-Jun-19	01-Jul-19					
Inlet Work, Preliminary Treatment Works and Inlet Pumping Station (PTW & IPS)									
CS1220	Substructure (rc structure)	203	26-Oct-18 A	16-May-19					
CS1224	Removal of ELS	4	16-May-19	20-May-19					
CS1226	Backfilling (except in Water Tightness Test area)	2	20-May-19	22-May-19					
CS1230	Superstructure (rc and metalworks)	131	11-Jan-19 A	22-May-19					

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 4 OF 11					
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019					
					Apr	May	Jun	Jul	Aug	
CS1236	Water Tightness Test + Backfilling	25	26-May-19	20-Jun-19						Water Tightness Test + Backfilling
CS1240	ABWF - Preliminary Treatment Works and Inlet Pumping Station	10	10-Jun-19	20-Jun-19						ABWF - Preliminary Treatment Works and Inlet Pumping Station
Solid Handling Building (SHB)		73	02-May-19	14-Jul-19						
CS1300	Substructure (rc structure)	23	02-May-19	25-May-19						Substructure (rc structure)
CS1305	Backfilling (except in Water Tightness Test area)	6	08-Jul-19	14-Jul-19						Backfilling (except in Water Tightness Test area)
CS1310	Superstructure (rc and metalworks)	35	26-May-19	30-Jun-19						Superstructure (rc and metalworks)
CS1315	Water Tightness Test + Backfilling	25	26-May-19	20-Jun-19						Water Tightness Test + Backfilling
CS1320	ABWF - Solid Handling Building	24	20-Jun-19	14-Jul-19						ABWF - Solid Handling Building
UV Disinfection Facility (UV)		166	01-Jan-19 A	15-Jun-19						
CS1915	Backfilling (except in Water Tightness Test area)	144	01-Jan-19 A	25-May-19						Backfilling (except in Water Tightness Test area)
CS1925	Water Tightness Test + Backfilling	22	05-May-19	26-May-19						Water Tightness Test + Backfilling
CS1930	ABWF - UV Disinfection Facility	47	30-Apr-19	15-Jun-19						ABWF - UV Disinfection Facility
Sludge Dewatering Building (SDB)		198	27-Nov-18 A	12-Jun-19						
CS1836	Backfilling (except in Water Tightness Test area)	12	01-Jun-19	12-Jun-19						Backfilling (except in Water Tightness Test area)
CS1845	Water Tightness Test + Backfilling	153	02-Jan-19 A	04-Jun-19						Water Tightness Test + Backfilling
CS1850	ABWF - Sludge Dewatering Building	198	27-Nov-18 A	12-Jun-19						ABWF - Sludge Dewatering Building
Sludge Skip Storage Building (SSSB)		61	15-Jun-19	14-Aug-19						
CS2900	Substructure (rc structure)	24	15-Jun-19	08-Jul-19						Substructure (rc structure)
CS2905	Backfilling	2	09-Jul-19	10-Jul-19						Backfilling
CS2910	Superstructure (rc and metalworks)	37	09-Jul-19	14-Aug-19						Superstructure (rc and metalworks)
LOT #2 - Bldg / Facilities Const. (Arch'l & Strud'l) : AB+WS, DO, CB, FH		484	03-Apr-18 A	30-Jul-19						
Administration Building & Maintenance Workshop (AB & WS)		428	03-Apr-18 A	04-Jun-19						
CS1115	Backfilling	414	03-Apr-18 A	21-May-19						Backfilling
CS1125	Water Tightness Test	121	18-Jan-19 A	19-May-19						Water Tightness Test
CS1130	ABWF - Administration Building & Maintenance Workshop	166	21-Dec-18 A	04-Jun-19						ABWF - Administration Building & Maintenance Workshop
Deodorization Facilities No. 1 (DO 1)		32	15-Jun-19	16-Jul-19						
CS1610	Substructure (rc structure)	21	15-Jun-19	05-Jul-19						Substructure (rc structure)
CS1615	Backfilling	2	06-Jul-19	07-Jul-19						Backfilling
CS1620	Superstructure (rc and metalworks)	7	06-Jul-19	12-Jul-19						Superstructure (rc and metalworks)
CS1630	ABWF - Deodorization Facilities No.1	6	10-Jul-19	16-Jul-19						ABWF - Deodorization Facilities No.1
Deodorization Facilities No. 2 (DO 2)		46	15-Jun-19	30-Jul-19						
CS1710	Substructure (rc structure)	30	15-Jun-19	14-Jul-19						Substructure (rc structure)
CS1715	Backfilling	2	15-Jul-19	16-Jul-19						Backfilling
CS1720	Superstructure (rc and metalworks)	9	15-Jul-19	23-Jul-19						Superstructure (rc and metalworks)
CS1730	ABWF - Deodorization Facilities No.2	7	24-Jul-19	30-Jul-19						ABWF - Deodorization Facilities No.2
Chemical Building (CB)		117	26-Feb-19 A	22-Jun-19						
CS2315	Backfilling	4	30-Apr-19	03-May-19						Backfilling
CS2320	Superstructure (rc and metalworks)	68	26-Feb-19 A	04-May-19						Superstructure (rc and metalworks)
CS2330	ABWF - Chemical Building	52	02-May-19	22-Jun-19						ABWF - Chemical Building
Street Fire Hydrant Pump Room & GENSET Room (FH)		74	18-Apr-19 A	30-Jun-19						
CS3010	Substructure (rc structure)	23	18-Apr-19 A	10-May-19						Substructure (rc structure)
CS3015	Backfilling	2	11-May-19	12-May-19						Backfilling
CS3020	Superstructure (rc and metalworks)	32	11-May-19	11-Jun-19						Superstructure (rc and metalworks)
CS3025	Water Tightness Test	24	07-Jun-19	30-Jun-19						Water Tightness Test
CS3030	ABWF - Street Fire Hydrant Pump Room & GENSET Room	14	17-Jun-19	30-Jun-19						ABWF - Street Fire Hydrant Pump Room & GENSET Room
LOT #3 - Bldg / Facilities Const. (Arch'l & Strud'l) : EB, RW, DG, ICW, JC		215	26-Feb-19 A	28-Sep-19						

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 5 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
Electrical Building No.1 (EB1)									
CS2415	Backfilling	76	26-Feb-19 A	13-May-19		Backfilling			
CS2420	Superstructure (rc and metalworks)	64	26-Feb-19 A	01-May-19	Superstructure (rc and metalworks)				
CS2430	ABWF - Electrical Building No.1	27	16-Apr-19 A	13-May-19	ABWF - Electrical Building No.1				
Electrical Building No.2 (EB2)									
CS2515	Backfilling	3	06-May-19	08-May-19		Backfilling			
CS2530	ABWF - Electrical Building No.2	32	14-Apr-19 A	15-May-19	ABWF - Electrical Building No.2				
Electrical Building No.3 (EB3)									
CS2615	Backfilling	6	04-May-19	09-May-19		Backfilling			
CS2630	ABWF - Electrical Building No.3	26	20-Apr-19 A	16-May-19	ABWF - Electrical Building No.3				
Electrical Building No.4 (EB4)									
CS2715	Backfilling	2	30-Apr-19	01-May-19		Backfilling			
CS2730	ABWF - Electrical Building No.4	29	10-Apr-19 A	08-May-19	ABWF - Electrical Building No.4				
Re-use Water Building (RW)									
CS2010	Substructure (rc structure)	16	30-Apr-19	15-May-19		Substructure (rc structure)			
CS2015	Backfilling (except in Water Tightness Test area)	1	16-May-19	16-May-19		Backfilling (except in Water Tightness Test area)			
CS2020	Superstructure (rc and metalworks)	32	16-May-19	16-Jun-19		Superstructure (rc and metalworks)			
CS2025	Water Tightness Test + Backfilling	9	14-Jun-19	22-Jun-19		Water Tightness Test + Backfilling			
CS2030	ABWF - Re-use Water Building	7	21-Jun-19	27-Jun-19		ABWF - Re-use Water Building			
Existing Junction Chamber (JC)									
CS2210	Bar Screen Installation	120	01-Jun-19	28-Sep-19					
LOT #4 - Bldg / Facilities Const. (Arch'l & Struct'l) : GH, PF, FW									
Payment Flowmeter Chamber (PF)									
CS2105	Backfilling	4	19-May-19	22-May-19		Backfilling			
CS2115	Water Tightness Test + Backfilling	22	01-May-19	22-May-19		Water Tightness Test + Backfilling			
CS2120	ABWF - Payment Flowmeter Chamber	40	14-May-19	22-Jun-19		ABWF - Payment Flowmeter Chamber			
Foul Water Pump Sump (FW)									
CS3395	Substructure (rc structure)	37	11-May-19	16-Jun-19		Substructure (rc structure)			
CS3405	Superstructure (rc and metalworks)	9	08-Jun-19	16-Jun-19		Superstructure (rc and metalworks)			
External Works & Miscellaneous									
CS3200	Site Formation along Boundary Wall (Perimeter)	180	08-May-19	04-Nov-19					
CS3201	Slope works and Retaining Wall (Eastern Portion)	484	04-Jul-18 A	30-Oct-19					
CS3203	Slope works and Retaining Wall (Northern Portion)	484	04-Jul-18 A	30-Oct-19					
CS3210	Drainage Inlet connection (Diversion of Three Existing Sewage Rising Mains) incl. slope & retaining wall work @ P8	120	01-Jul-19	28-Oct-19					
CS3225	Drainage Outlet connection to the Existing Stormwater Drainage System along Ha Tsuen Road	92	16-May-19	16-Aug-19					
CS3230	CLP Cable Duct and Draw Pits (within the Site)	100	21-May-19	28-Aug-19					
CS3250	EVA (Road & Drainage)	715	29-Jun-18 A	12-Jun-20					
CS3252	RC Trench and Odour Pipe (DO1, DO2)	121	30-Apr-19	28-Aug-19					
CS3254	Process Pipe	121	08-May-19	05-Sep-19					
CS3256	Drainage Pipe (Stormwater) incl. Surface Drainage at Site Platform & On Slope	121	30-Jul-19	27-Nov-19					
CS3258	Emergency By-Pass Pipe	445	15-Jul-18 A	02-Oct-19					
CS3260	Sewage Pipe	314	14-Dec-18 A	23-Oct-19					
CS3262	Cable Duct and Draw Pits	180	30-Apr-19	26-Oct-19					
CS3276	WSD External Watermain Laying Works	180	11-May-19	06-Nov-19					
CS3278	Internal Watermain Laying Works	150	11-May-19	07-Oct-19					
Green Roof									
		78	05-Jun-19	21-Aug-19					

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 6 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
CS3340	Administration Building and Maintenance Workshop	60	05-Jun-19	03-Aug-19					Administration Building
CS3350	Sludge Dewatering Building	60	13-Jun-19	11-Aug-19					Sludge Dewatering
CS3360	Chemical Building	60	23-Jun-19	21-Aug-19					Chemical Building
Statutory Works		266	30-Apr-19	21-Jan-20					
Electrical Supply & Energization - CLP		122	30-Apr-19	29-Aug-19					
SR100	Enabling Works for Handover of EB1 Transformer Rooms to CLP	30	01-Jun-19	30-Jun-19					Enabling Works for Handover of EB1 Transformer Rooms to CLP
SR105	CLP Works in EB1 Transformer Rooms	60	01-Jul-19	29-Aug-19					
SR110	LV Switchboard Installation & Cabling Works in EB1 Switch Rooms	55	30-Jun-19	23-Aug-19					LV Switchboard Installation & Cabling Works in EB1 Switch Rooms
SR115	Enabling Works for Handover of EB3 Transformer Room to CLP	40	30-Apr-19	08-Jun-19					Enabling Works for Handover of EB3 Transformer Room to CLP
SR120	CLP Works in EB3 Transformer Room	60	01-Jul-19	29-Aug-19					
SR125	LV Switchboard Installation & Cabling Works in EB3 Switch Room	60	26-Jun-19	24-Aug-19					LV Switchboard Installation & Cabling Works in EB3 Switch Room
SR140	CLP Internal Cabling Works	80	11-Jun-19	29-Aug-19					
Fire Services - FSD		215	20-Jun-19	21-Jan-20					
SR300	F5 Pump Room & Tank Installation (FH)	185	20-Jun-19	22-Dec-19					
SR302	F5 Pump Room & Tank Installation (AB)	185	20-Jul-19	21-Jan-20					
Generator - EPD		120	01-Jul-19	28-Oct-19					
SR600	Emergency Generator Installation	120	01-Jul-19	28-Oct-19					
SR610	Submission to EPD for Genset Exhaust Pipe	0	01-Jul-19						Submission to EPD for Genset Exhaust Pipe
E&M Works		1171	27-Nov-16 A	10-Feb-20					
Procurement		1032	27-Nov-16 A	24-Sep-19					
Chemically Enhanced Primary Treatment (CEPT)		631	10-Nov-17 A	02-Aug-19					
EM3112	Manufacturing & Logistic (Major Equipment)	440	21-Feb-18 A	07-May-19					Manufacturing & Logistic (Major Equipment)
EM3116	Manufacturing & Logistic (Penstock, Pipe & Valve)	177	29-Nov-18 A	25-May-19					Manufacturing & Logistic (Penstock, Pipe & Valve)
EM3118	CMS Preparation, Submission & Approval (Electrical)	547	10-Nov-17 A	10-May-19					CMS Preparation, Submission & Approval (Electrical)
EM3120	Manufacturing & Logistic (Electrical)	247	29-Nov-18 A	02-Aug-19					Manufacturing & Logistic (Electrical)
EM3122	CMS Preparation, Submission & Approval (Building Services)	548	10-Nov-17 A	12-May-19					CMS Preparation, Submission & Approval (Building Services)
EM3124	Manufacturing & Logistic (Building Services)	236	29-Nov-18 A	22-Jul-19					Manufacturing & Logistic (Building Services)
System Control Flowmeter Chamber (SF)		626	10-Nov-17 A	28-Jul-19					
EM3134	Manufacturing & Logistic (Major Equipment)	281	28-Sep-18 A	05-Jul-19					Manufacturing & Logistic (Major Equipment)
EM3138	Manufacturing & Logistic (Penstock, Pipe & Valve)	168	29-Nov-18 A	16-May-19					Manufacturing & Logistic (Penstock, Pipe & Valve)
EM3140	CMS Preparation, Submission & Approval (Electrical)	548	10-Nov-17 A	11-May-19					CMS Preparation, Submission & Approval (Electrical)
EM3142	Manufacturing & Logistic (Electrical)	215	29-Nov-18 A	01-Jul-19					Manufacturing & Logistic (Electrical)
EM3144	CMS Preparation, Submission & Approval (Building Services)	548	10-Nov-17 A	12-May-19					CMS Preparation, Submission & Approval (Building Services)
EM3146	Manufacturing & Logistic (Building Services)	242	29-Nov-18 A	28-Jul-19					Manufacturing & Logistic (Building Services)
Inlet Work, Preliminary Treatment Units and Inlet Pumping Station (PTW & IPS)		951	04-Jan-17 A	13-Aug-19					
EM3135	CMS Preparation, Submission & Approval (Major Equipment)	850	04-Jan-17 A	04-May-19					CMS Preparation, Submission & Approval (Major Equipment)
EM3137	Manufacturing & Logistic (Major Equipment)	246	10-Dec-18 A	13-Aug-19					Manufacturing & Logistic (Major Equipment)
EM3141	Witness FAT - Main Sewage Pumps	28	30-Apr-19	27-May-19					Witness FAT - Main Sewage Pumps
EM3635	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	580	01-Oct-17 A	04-May-19					CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)
EM3645	Manufacturing & Logistic (Penstock, Pipe & Valve)	243	11-Dec-18 A	11-Aug-19					Manufacturing & Logistic (Penstock, Pipe & Valve)
EM3655	CMS Preparation, Submission & Approval (Electrical)	579	01-Oct-17 A	02-May-19					CMS Preparation, Submission & Approval (Electrical)
EM3665	Manufacturing & Logistic (Electrical)	217	05-Dec-18 A	09-Jul-19					Manufacturing & Logistic (Electrical)
EM3675	CMS Preparation, Submission & Approval (Building Services)	582	01-Oct-17 A	06-May-19					CMS Preparation, Submission & Approval (Building Services)
EM3685	Manufacturing & Logistic (Building Services)	247	02-Dec-18 A	06-Aug-19					Manufacturing & Logistic (Building Services)
Solid Handling Building (SHB)		848	12-Apr-17 A	07-Aug-19					
EM3145	CMS Preparation, Submission & Approval (Major Equipment)	751	12-Apr-17 A	02-May-19					CMS Preparation, Submission & Approval (Major Equipment)

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 7 OF 11					
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019					
					Apr	May	Jun	Jul	Aug	
EM3150	Manufacturing & Logistic (Major Equipment)	210	11-Nov-18 A	09-Jun-19						Manufacturing & Logistic (Major Equipment)
EM3695	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	580	01-Oct-17 A	04-May-19						CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)
EM3705	Manufacturing & Logistic (Penstock, Pipe & Valve)	199	11-Nov-18 A	29-May-19						Manufacturing & Logistic (Penstock, Pipe & Valve)
EM3715	CMS Preparation, Submission & Approval (Electrical)	579	01-Oct-17 A	03-May-19						CMS Preparation, Submission & Approval (Electrical)
EM3725	Manufacturing & Logistic (Electrical)	213	10-Dec-18 A	11-Jul-19						Manufacturing & Logistic (Electrical)
EM3735	CMS Preparation, Submission & Approval (Building Services)	580	01-Oct-17 A	04-May-19						CMS Preparation, Submission & Approval (Building Services)
EM3745	Manufacturing & Logistic (Building Services)	241	10-Dec-18 A	07-Aug-19						Manufacturing & Logistic (Building Services)
UV Disinfection Facility (UV)		629	21-Nov-17 A	12-Aug-19						
EM3190	Manufacturing & Logistic (Major Equipment)	432	30-Apr-18 A	06-Jul-19						Manufacturing & Logistic (Major Equipment)
EM3192	Delivery To Site (Major Equipment)	215	10-Dec-18 A	12-Jul-19						Delivery To Site (Major Equipment)
EM3765	Manufacturing & Logistic (Penstock, Pipe & Valve)	201	12-Dec-18 A	30-Jun-19						Manufacturing & Logistic (Penstock, Pipe & Valve)
EM3775	CMS Preparation, Submission & Approval (Electrical)	531	21-Nov-17 A	05-May-19						CMS Preparation, Submission & Approval (Electrical)
EM3785	Manufacturing & Logistic (Electrical)	211	12-Dec-18 A	11-Jul-19						Manufacturing & Logistic (Electrical)
EM3795	CMS Preparation, Submission & Approval (Building Services)	541	21-Nov-17 A	15-May-19						CMS Preparation, Submission & Approval (Building Services)
EM3805	Manufacturing & Logistic (Building Services)	214	10-Jan-19 A	12-Aug-19						Manufacturing & Logistic (Building Services)
Sludge Dewatering Building (SDB)		1023	27-Nov-16 A	15-Sep-19						
EM3175	CMS Preparation, Submission & Approval (Major Equipment)	897	27-Nov-16 A	13-May-19						CMS Preparation, Submission & Approval (Major Equipment)
EM3180	Manufacturing & Logistic (Major Equipment)	305	27-Oct-18 A	27-Aug-19						Manufacturing & Logistic (Major Equipment)
EM3815	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	563	27-Oct-17 A	13-May-19						CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)
EM3825	Manufacturing & Logistic (Penstock, Pipe & Valve)	182	01-Mar-19 A	29-Aug-19						Manufacturing & Logistic (Penstock, Pipe & Valve)
EM3835	CMS Preparation, Submission & Approval (Electrical)	553	27-Oct-17 A	02-May-19						CMS Preparation, Submission & Approval (Electrical)
EM3845	Manufacturing & Logistic (Electrical)	186	29-Nov-18 A	03-Jun-19						Manufacturing & Logistic (Electrical)
EM3855	CMS Preparation, Submission & Approval (Building Services)	569	27-Oct-17 A	18-May-19						CMS Preparation, Submission & Approval (Building Services)
EM3865	Manufacturing & Logistic (Building Services)	120	19-May-19	15-Sep-19						Manufacturing & Logistic (Building Services)
Sludge Skip Storage Building (SSSB)		642	04-Sep-17 A	08-Jun-19						
EM3875	CMS Preparation, Submission & Approval (Electrical)	603	04-Sep-17 A	30-Apr-19						CMS Preparation, Submission & Approval (Electrical)
EM3885	Manufacturing & Logistic (Electrical)	191	29-Nov-18 A	08-Jun-19						Manufacturing & Logistic (Electrical)
EM3895	CMS Preparation, Submission & Approval (Building Services)	603	04-Sep-17 A	30-Apr-19						CMS Preparation, Submission & Approval (Building Services)
EM3905	Manufacturing & Logistic (Building Services)	181	29-Nov-18 A	29-May-19						Manufacturing & Logistic (Building Services)
Administration Building & Maintenance Workshop (AB & WS)		890	31-Jan-17 A	09-Jul-19						
EM3125	CMS Preparation, Submission & Approval (Major Equipment)	831	31-Jan-17 A	11-May-19						CMS Preparation, Submission & Approval (Major Equipment)
EM3130	Manufacturing & Logistic (Major Equipment)	212	29-Nov-18 A	28-Jun-19						Manufacturing & Logistic (Major Equipment)
EM3915	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	621	30-Aug-17 A	12-May-19						CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)
EM3925	Manufacturing & Logistic (Penstock, Pipe & Valve)	200	29-Nov-18 A	17-Jun-19						Manufacturing & Logistic (Penstock, Pipe & Valve)
EM3935	CMS Preparation, Submission & Approval (Electrical)	621	30-Aug-17 A	12-May-19						CMS Preparation, Submission & Approval (Electrical)
EM3945	Manufacturing & Logistic (Electrical)	223	29-Nov-18 A	09-Jul-19						Manufacturing & Logistic (Electrical)
EM3955	CMS Preparation, Submission & Approval (Building Services)	621	30-Aug-17 A	12-May-19						CMS Preparation, Submission & Approval (Building Services)
EM3965	Manufacturing & Logistic (Building Services)	223	29-Nov-18 A	09-Jul-19						Manufacturing & Logistic (Building Services)
Deodorization Facilities No. 1 & 2 (DO 1 & DO 2)		988	10-Jan-17 A	24-Sep-19						
EM3165	CMS Preparation, Submission & Approval (Major Equipment)	851	10-Jan-17 A	10-May-19						CMS Preparation, Submission & Approval (Major Equipment)
EM3170	Manufacturing & Logistic (Major Equipment)	181	27-Nov-18 A	27-May-19						Manufacturing & Logistic (Major Equipment)
EM3171	Witness FAT - DO 1 & DO 2	167	27-Nov-18 A	12-May-19						Witness FAT - DO 1 & DO 2
EM3172	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	621	30-Aug-17 A	12-May-19						CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)
EM3173	Manufacturing & Logistic (Penstock, Pipe & Valve)	214	27-Nov-18 A	29-Jun-19						Manufacturing & Logistic (Penstock, Pipe & Valve)
EM3975	CMS Preparation, Submission & Approval (Electrical)	621	30-Aug-17 A	12-May-19						CMS Preparation, Submission & Approval (Electrical)
EM3985	Manufacturing & Logistic (Electrical)	201	27-Nov-18 A	16-Jun-19						Manufacturing & Logistic (Electrical)
EM3995	CMS Preparation, Submission & Approval (Building Services)	636	30-Aug-17 A	27-May-19						CMS Preparation, Submission & Approval (Building Services)

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 8 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
EM4005	Manufacturing & Logistic (Building Services)	120	27-May-19	24-Sep-19					
Chemical Building (CB)									
EM3230	Manufacturing & Logistic (Major Equipment)	412	08-Nov-17 A	30-Jun-19					
EM4025	Manufacturing & Logistic (Penstock, Pipe & Valve)	172	12-Dec-18 A	01-Jun-19					
EM4045	Manufacturing & Logistic (Electrical)	187	12-Dec-18 A	17-Jun-19					
EM4055	CMS Preparation, Submission & Approval (Building Services)	542	08-Nov-17 A	04-May-19					
EM4065	Manufacturing & Logistic (Building Services)	200	12-Dec-18 A	30-Jun-19					
Street Fire Hydrant Pump Room & GENSET Room (FH)									
EM3275	CMS Preparation, Submission & Approval (Major Equipment)	773	23-Mar-17 A	04-May-19					
EM3280	Manufacturing & Logistic (Major Equipment)	183	12-Dec-18 A	12-Jun-19					
EM4075	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	580	01-Oct-17 A	03-May-19					
EM4085	Manufacturing & Logistic (Penstock, Pipe & Valve)	218	12-Dec-18 A	18-Jun-19					
EM4095	CMS Preparation, Submission & Approval (Electrical)	582	01-Oct-17 A	05-May-19					
EM4105	Manufacturing & Logistic (Electrical)	196	12-Dec-18 A	25-Jun-19					
EM4115	CMS Preparation, Submission & Approval (Building Services)	588	01-Oct-17 A	12-May-19					
EM4125	Manufacturing & Logistic (Building Services)	206	12-Dec-18 A	06-Jun-19					
Electrical Buildings (EB1, EB2, EB3 & EB4)									
EM3235	CMS Preparation, Submission & Approval (Major Equipment)	800	23-Feb-17 A	03-May-19					
EM3240	Manufacturing & Logistic (Major Equipment)	184	08-Dec-18 A	10-Jun-19					
EM3245	Witness FAT - LV Switchboards (8 nos. for EB's and 4 nos. for SDB)	21	30-Apr-19	20-May-19					
EM3300	CMS Preparation, Submission & Approval (Electrical)	599	11-Sep-17 A	03-May-19					
EM3305	Manufacturing & Logistic (Electrical)	183	08-Dec-18 A	08-Jun-19					
EM3310	CMS Preparation, Submission & Approval (Control & Instrument)	601	11-Sep-17 A	05-May-19					
EM3315	Manufacturing & Logistic (Control & Instrument)	190	08-Dec-18 A	16-Jun-19					
EM3320	CMS Preparation, Submission & Approval (Building Services)	630	09-Aug-17 A	30-Apr-19					
EM3325	Manufacturing & Logistic (Building Services)	199	08-Dec-18 A	24-Jun-19					
Re-use Water Building (RW)									
EM3200	Manufacturing & Logistic (Major Equipment)	317	28-Jun-18 A	11-May-19					
EM4145	Manufacturing & Logistic (Penstock, Pipe & Valve)	193	15-Nov-18 A	27-May-19					
EM4155	CMS Preparation, Submission & Approval (Electrical)	529	19-Nov-17 A	02-May-19					
EM4165	Manufacturing & Logistic (Electrical)	194	12-Dec-18 A	23-Jun-19					
EM4175	CMS Preparation, Submission & Approval (Building Services)	531	19-Nov-17 A	03-May-19					
EM4185	Manufacturing & Logistic (Building Services)	206	12-Dec-18 A	06-Jun-19					
DG Store & Chemical Waste Storage Building (DG) and Irrigation & Cleansing Water Pump Room (ICW)									
EM3255	CMS Preparation, Submission & Approval (Major Equipment)	709	24-May-17 A	02-May-19					
EM3260	Manufacturing & Logistic (Major Equipment)	194	12-Dec-18 A	23-Jun-19					
EM4195	CMS Preparation, Submission & Approval (Penstock, Pipe & Valve)	512	10-Dec-17 A	05-May-19					
EM4205	Manufacturing & Logistic (Penstock, Pipe & Valve)	166	12-Dec-18 A	27-May-19					
EM4215	CMS Preparation, Submission & Approval (Electrical)	579	30-Sep-17 A	02-May-19					
EM4225	Manufacturing & Logistic (Electrical)	173	12-Dec-18 A	02-Jun-19					
EM4235	CMS Preparation, Submission & Approval (Building Services)	581	30-Sep-17 A	03-May-19					
EM4245	Manufacturing & Logistic (Building Services)	206	12-Dec-18 A	06-Jun-19					
Gatehouse (GH)									
EM3285	CMS Preparation, Submission & Approval (Building Services)	742	24-Apr-17 A	05-May-19					
EM3290	Manufacturing & Logistic (Building Services)	227	12-Dec-18 A	27-Jun-19					
Payment Flowmeter Chamber (PF)									
EM3210	Manufacturing & Logistic (Major Equipment)	268	28-Sep-18 A	22-Jun-19					

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (30-Apr-19)			PAGE 9 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
EM3211	Witness FAT - Payment Flowmeter and Reference Flowmeter	7	30-Apr-19	06-May-19					
EM4265	Manufacturing & Logistic (Penstock, Pipe & Valve)	196	11-Dec-18 A	24-Jun-19					
EM4275	CMS Preparation, Submission & Approval (Electrical)	528	20-Nov-17 A	01-May-19					
EM4285	Manufacturing & Logistic (Electrical)	202	02-Dec-18 A	21-Jun-19					
EM4295	CMS Preparation, Submission & Approval (Building Services)	538	20-Nov-17 A	11-May-19					
EM4305	Manufacturing & Logistic (Building Services)	98	11-May-19	17-Aug-19					
SCADA and CMMS Systems		784	01-Jul-17 A	24-Aug-19					
EM3330	CMS Preparation, Submission & Approval	670	01-Jul-17 A	02-May-19					
EM3335	Manufacturing & Logistic (SCADA)	203	12-Dec-18 A	02-Jul-19					
EM3340	Witness FAT - SCADA System	28	30-Apr-19	27-May-19					
EM3345	Manufacturing & Logistic (CMMS)	112	04-May-19	24-Aug-19					
EM3350	Witness FAT - CMMS	14	17-May-19	31-May-19					
Installation		340	08-Mar-19 A	10-Feb-20					
Chemically Enhanced Primary Treatment (CEPT)		176	30-Apr-19	22-Oct-19					
EM1500	Plant (Mechanical) Installation	142	30-Apr-19	18-Sep-19					
EM1505	Pipeworks	120	25-Jun-19	22-Oct-19					
EM1507	FRP Covers	90	25-Jun-19	22-Oct-19					
EM1510	Electrical Installation	75	25-Jun-19	07-Sep-19					
EM1515	Cabling Works	120	25-Jun-19	22-Oct-19					
EM1520	BS - Electrical	90	25-Jun-19	22-Oct-19					
EM1525	BS - MVAC Installation	120	25-Jun-19	22-Oct-19					
EM1530	BS - FS Installation	90	25-Jun-19	22-Oct-19					
EM1535	BS - Plumbing and Drainage Installation	120	25-Jun-19	22-Oct-19					
System Control Flowmeter Chamber (SF)		60	21-Jul-19	19-Sep-19					
EM1400	Plant (Mechanical) Installation	60	21-Jul-19	19-Sep-19					
EM1405	Pipeworks	60	21-Jul-19	19-Sep-19					
Inlet Work, Preliminary Treatment Units and Inlet Pumping Station (PTW & IPS)		200	29-Jun-19	15-Jan-20					
EM1200	Plant (Mechanical) Installation	180	29-Jun-19	26-Dec-19					
EM1205	Pipeworks	180	19-Jul-19	15-Jan-20					
Solid Handling Building (SHB)		90	14-Jul-19	12-Oct-19					
EM1300	Plant (Mechanical) Installation	90	14-Jul-19	12-Oct-19					
UV Disinfection Facility (UV)		240	16-Jun-19	10-Feb-20					
EM1900	Plant (Mechanical) Installation	240	16-Jun-19	10-Feb-20					
Sludge Dewatering Building (SDB)		261	18-Mar-19 A	03-Dec-19					
EM1800	Plant (Mechanical) Installation	226	18-Mar-19 A	29-Oct-19					
EM1810	Electrical Installation	97	01-Apr-19 A	06-Jul-19					
EM1815	Cabling Works	150	06-Jul-19	03-Dec-19					
Administration Building & Maintenance Workshop (AB & WS)		299	18-Mar-19 A	11-Jan-20					
EM1100	SCADA System	180	30-Apr-19	26-Oct-19					
EM1105	Plant Installation (WS)	200	01-Apr-19 A	17-Oct-19					
EM1110	ELV System	180	30-Apr-19	26-Oct-19					
EM1120	BS - MVAC Installation	205	18-Mar-19 A	08-Oct-19					
EM1130	Passenger Lift	180	30-Apr-19	26-Oct-19					
EM1140	BS - FS System & Control	209	01-Apr-19 A	26-Oct-19					
EM1145	BS - Electrical	206	01-Apr-19 A	24-Oct-19					
EM1150	BS - Plumbing and Drainage	180	06-May-19	02-Nov-19					
EM1160	Cabling Works	240	16-May-19	11-Jan-20					

DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 10 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
Deodorization Facilities No. 1 (DO 1)									
EM1600	Plant (Mechanical) Installation	90	16-Jul-19	14-Oct-19					
Chemical Building (CB)									
EM2300	Plant (Mechanical) Installation	120	23-Jun-19	20-Oct-19					
Street Fire Hydrant Pump Room & GENSET Room (FH)									
EM2900	Plant (Mechanical) Installation	120	10-Jul-19	06-Nov-19					
Electrical Building No.1 (EB1)									
EM2400	Electrical Installation	90	17-Jun-19	15-Sep-19					
EM2410	Cabling Works	90	07-Jul-19	05-Oct-19					
EM2420	BS - Electrical	60	02-Jul-19	31-Aug-19					
EM2425	BS - MVAC Installation	75	16-Jun-19	30-Aug-19					
EM2430	BS - FS Installation	60	02-Jul-19	31-Aug-19					
EM2435	BS - Plumbing and Drainage Installation	60	02-Jul-19	31-Aug-19					
Electrical Building No.2 (EB2)									
EM2500	Electrical Installation	90	17-Jun-19	15-Sep-19					
EM2510	Cabling Works	90	07-Jul-19	05-Oct-19					
EM2520	BS - Electrical	60	18-Jun-19	17-Aug-19					
EM2525	BS - MVAC Installation	75	16-Jun-19	30-Aug-19					
EM2530	BS - FS Installation	60	01-Jul-19	30-Aug-19					
EM2535	BS - Plumbing and Drainage Installation	60	01-Jul-19	30-Aug-19					
Electrical Building No.3 (EB3)									
EM2600	Electrical Installation	106	16-Jun-19	30-Sep-19					
EM2610	Cabling Works	90	27-Jun-19	25-Sep-19					
EM2620	BS - Electrical	60	02-Jul-19	31-Aug-19					
EM2625	BS - MVAC Installation	75	16-Jun-19	30-Aug-19					
EM2630	BS - FS Installation	60	02-Jul-19	31-Aug-19					
EM2635	BS - Plumbing and Drainage Installation	60	02-Jul-19	31-Aug-19					
Electrical Building No.4 (EB4)									
EM3400	Electrical Installation	207	08-Mar-19 A	30-Sep-19					
EM3410	Cabling Works	90	02-Jun-19	31-Aug-19					
EM3420	BS - Electrical	85	01-Apr-19 A	24-Jun-19					
EM3425	BS - MVAC Installation	111	08-Mar-19 A	26-Jun-19					
EM3430	BS - FS Installation	87	01-Apr-19 A	26-Jun-19					
EM3435	BS - Plumbing and Drainage Installation	60	07-May-19	06-Jul-19					
Re-use Water Building (RW)									
EM2000	Plant (Mechanical) Installation	140	28-Jun-19	14-Nov-19					
EM2015	Cabling Works	90	28-Jun-19	25-Sep-19					
DG Store & Chemical Waste Storage Building (DG) and Irrigation & Cleansing Water Pump Room (ICW)									
EM3450	Plant (Mechanical) Installation	120	18-Jul-19	14-Nov-19					
Payment Flowmeter Chamber (PF)									
EM2100	Plant (Mechanical) Installation	90	28-Jul-19	25-Oct-19					
EM2105	Pipeworks	120	23-Jun-19	20-Oct-19					
Testing & Commissioning									
TC005	Outlet Discharge Connection Completed	136	06-Mar-19 A	20-Jul-19					
TC030	Operation Plan - Preparation for Submission	0	20-Jul-19*						
TC035	Operation Plan - Submission to SO for Review and Approval	56	06-Mar-19 A	30-Apr-19					
		70	30-Apr-19	09-Jul-19					


DATA DATE: 30-Apr-19		LAYOUT: SW Project Phase 1 Rev 10 (3M 30Apr19)			PAGE 11 OF 11				
Activity ID	Activity Name	At Completion Duration	Start	Finish	2019				
					Apr	May	Jun	Jul	Aug
TC040	Asset Management Plan - Preparation for Submission	56	06-Mar-19 A	30-Apr-19	Asset Management Plan - Preparation for Submission				
TC045	Asset Management Plan - Submission to SO for Review and Approval	70	30-Apr-19	09-Jul-19	Asset Management Plan - Submission to SO for Review and Approval				

Appendix D1

Calibration Certificates for Impact Air Quality Monitoring Equipment

Summary of Calibration Certificates for TSP Monitoring Equipment used in this reporting month

Equip No.	Model	Serial No.	Calib Date	Due Date
ET/EA/001/05	Sibata LD-3B	8X4282	18/10/2018	17/04/2019
			15/04/2019	14/10/2019
ET/EA/001/08	Sibata LD-3B	135261	21/03/2019	20/09/2019
ET/EA/001/15	Sibata LD-3B	597227	17/01/2019	16/07/2019
ET/EA/003/12	Greasby GMW (GS2310)	9998	11/04/2019	10/06/2019
ET/EA/003/25	Greasby GMW (GS2310)	1934	11/04/2019	10/06/2019



Internal Calibration Report


of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration :** 18 October 2018

Serial No. : 8X4282 (ET/EA/001/05) **Calibration Due Date :** 17 April 2019

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition

Results :	Dust Monitor (CPM)	38	67	104
	High Volume Air Sampler (ug/m ³)	88	175	244
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 1 December 2018	

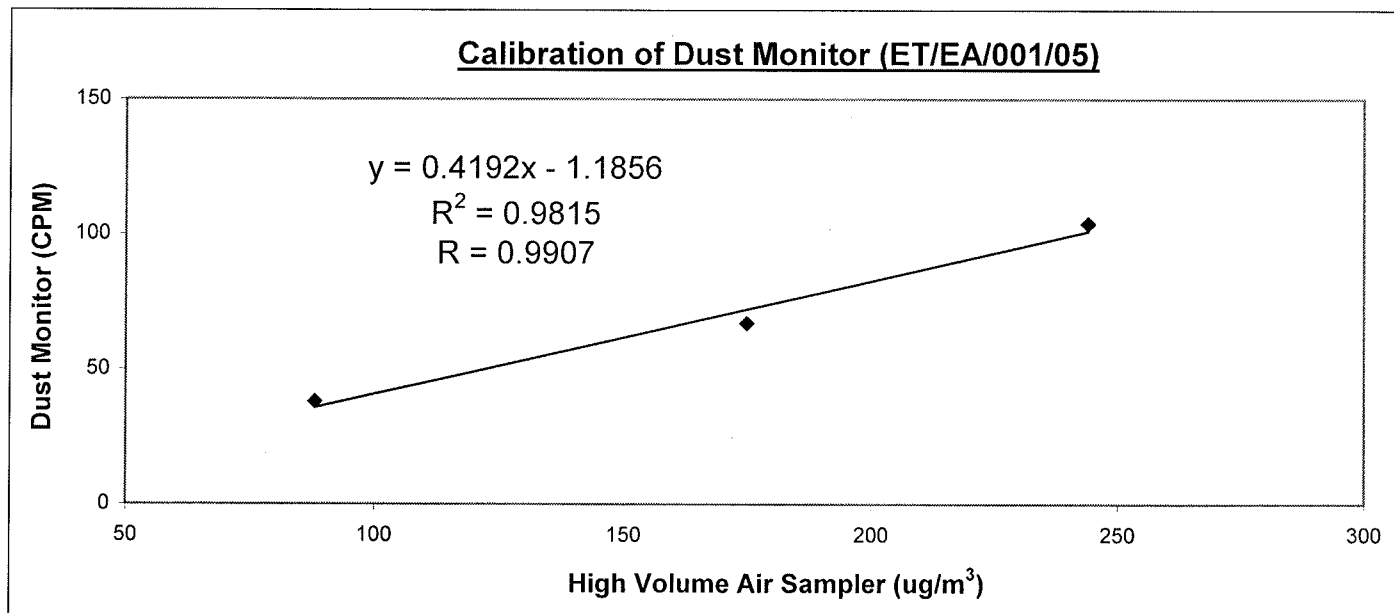


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / ~~unacceptable~~ * for use.


Calibrated by :


LI, Lok Yin
(Technician)

Checked by :


LAU, Chi Leung
(Environmental Team Leader)


- END OF REPORT -



Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 15 April 2019
Serial No. : 8X4282 (ET/EA/001/05) **Calibration Due Date** : 14 October 2019
Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition

Results :	Dust Monitor (CPM)	39	69	106
	TSP ($\mu\text{g}/\text{m}^3$)	85	171	240
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 28 May 2019	

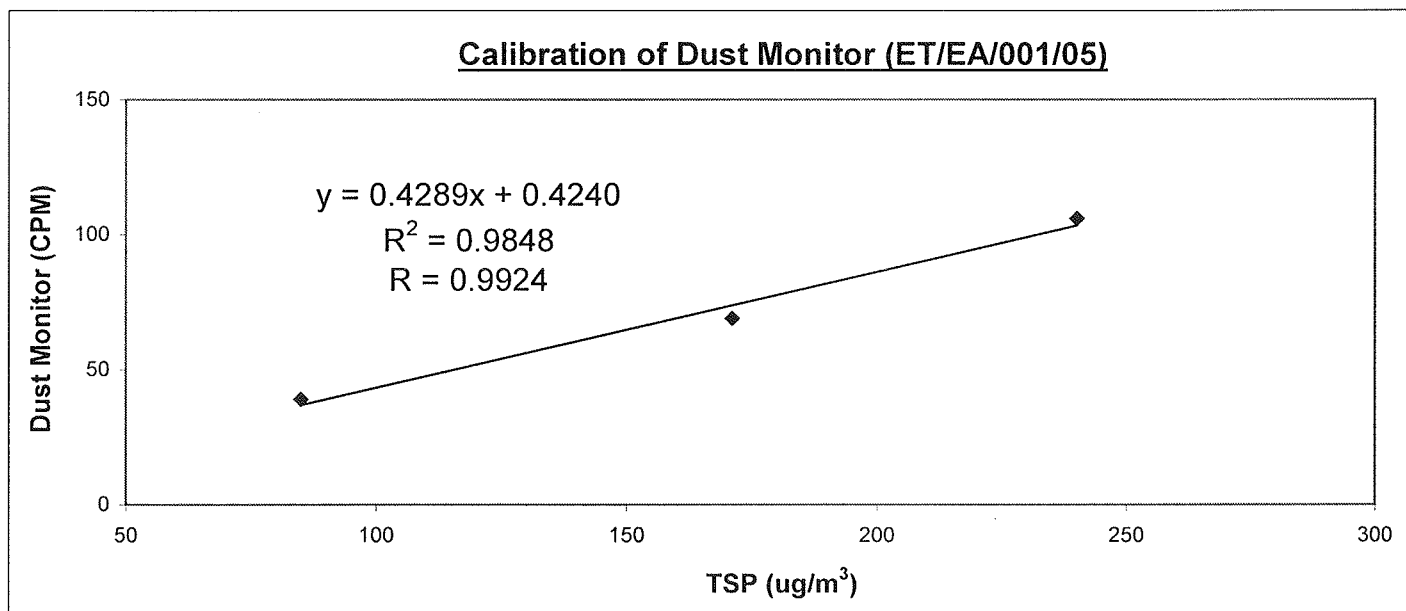


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : LI, Lok Yin
(Technician)

Checked by : LAU, Chi Leung
(Environmental Team Leader)

- END OF REPORT -



Internal Calibration Report


of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration :** 21 March 2019

Serial No. : 135261 (ET/EA/001/08) **Calibration Due Date :** 20 September 2019

Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Sampler together under the same environmental condition


Results :	Dust Monitor (CPM)	38	70	183
	High Volume Air Sampler ($\mu\text{g}/\text{m}^3$)	54	118	266
	High Volume Air Sampler Serial No.: 1177		Calibration Due Date: 29 March 2019	

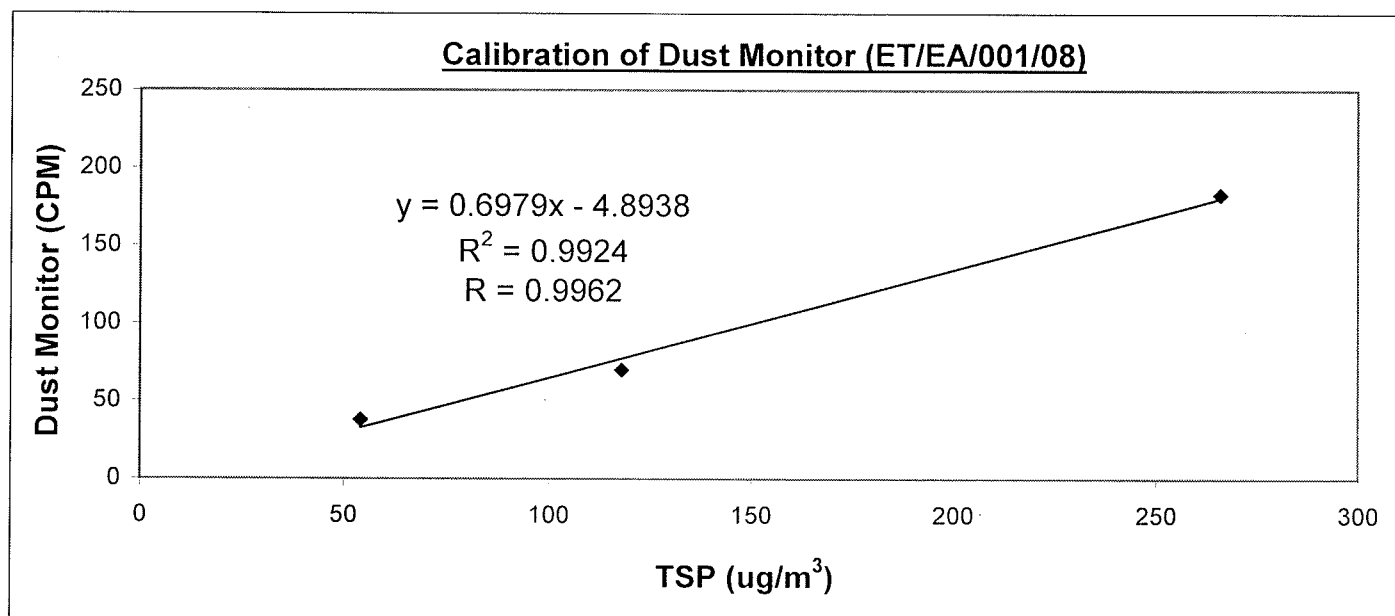


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / ~~unacceptable~~ * for use.


Calibrated by :


Li Lok Yin
(Technician)

Checked by :


LAU, Chi Leung
(Environmental Team Leader)

- END OF REPORT -




Internal Calibration Report
of
Dust Monitor

Manufacturer : SIBATA (LD-3B) **Date of Calibration** : 17 Jan 2019

Serial No. : 597227 (ET/EA/001/15) **Calibration Due Date** : 16 July 2019


Method : Parallel measurement (Three-point calibration) by placing the Dust Monitor and High Volume Air Samper together under the same environmental condition

Results	Dust Monitor (CPM)	28	66	172
	TSP (ug/m ³)	34	112	263
	High Volume Air Sampler Serial No.: 1177 Calibration Due Date: 29 January 2019			

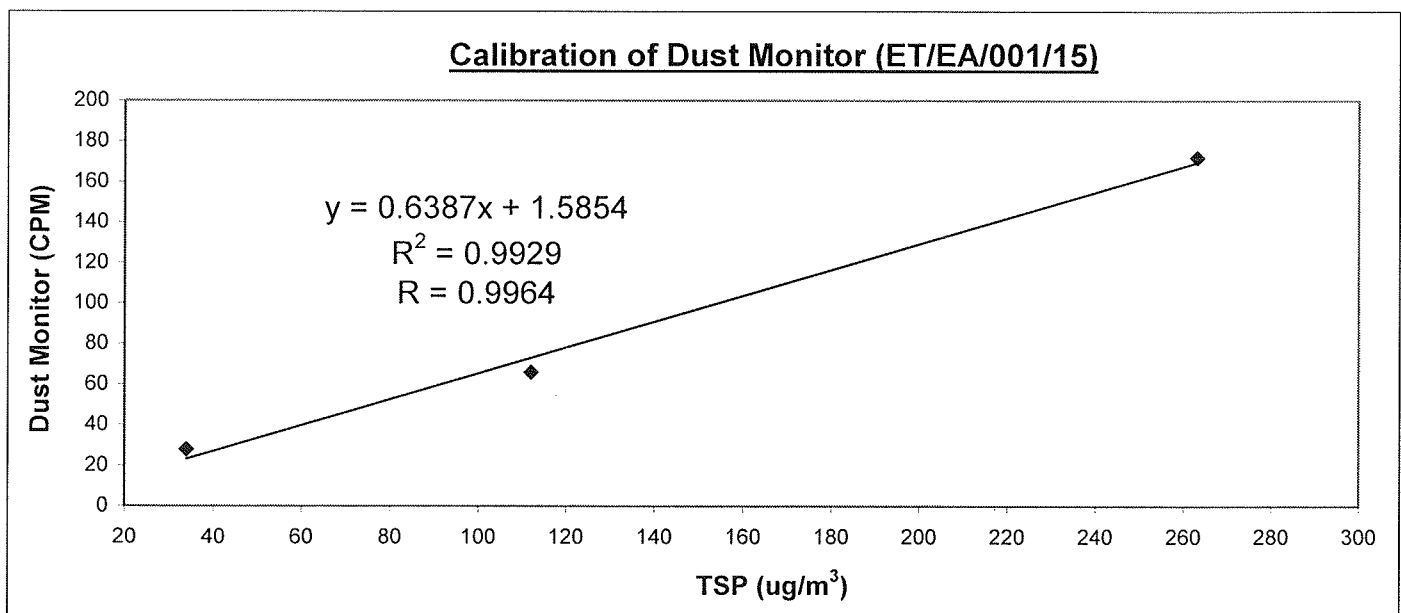


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a three-point calibration

The Dust Trak Monitor complies * / ~~does not comply~~ * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : 
LI, Lok Yin
(Technician)

Checked by : 
LAU, Chi Leung
(Environmental Team Leader)



Calibration Report
of
High Volume Air Sampler


Manufacturer : Graseby (Model No. GS2310) **Date of Calibration** : 14 February 2019

Serial No. : 1934 (ET / EA / 003 / 25) **Calibration Due Date** : 13 April 2019

Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual


Results :	Flow recorder reading (cfm)	55	48	39	36	26
	Qstd (Actual flow rate, m ³ /min)	1.86	1.67	1.40	1.19	0.89
	Pressure : 767.31 mm Hg	Temp. : 291 K				


Sampler 1934 Calibration Curve
Site: San Wai (ASR1a)

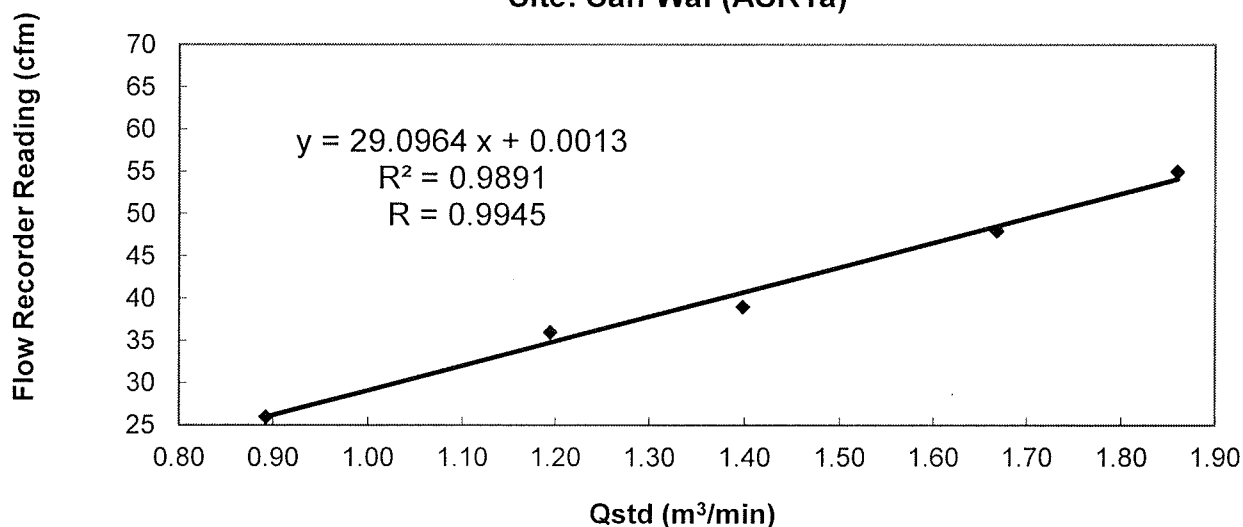


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.

The high volume sampler complies* / ~~does not comply*~~ with the specified requirements and is deemed acceptable* / unacceptable* for use.

Calibrated by : 
TANG, Chung Hang
(Supervisor)

Approved by : 
LAU, Chi Leung
(Environmental Team Leader)



Calibration Report
of
High Volume Air Sampler

Manufacturer : Graseby (Model No. GS2310) **Date of Calibration** : 11 April 2019


Serial No. : 1934 (ET / EA / 003 / 25) **Calibration Due Date** : 10 June 2019

Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results

Flow recorder reading (cfm)	54	48	39	35	26
Qstd (Actual flow rate, m ³ /min)	1.78	1.61	1.34	1.14	0.84
Pressure :	767.31 mm Hg		Temp. :	301 K	

Sampler 1934 Calibration Curve
Site: San Wai (ASR1a)

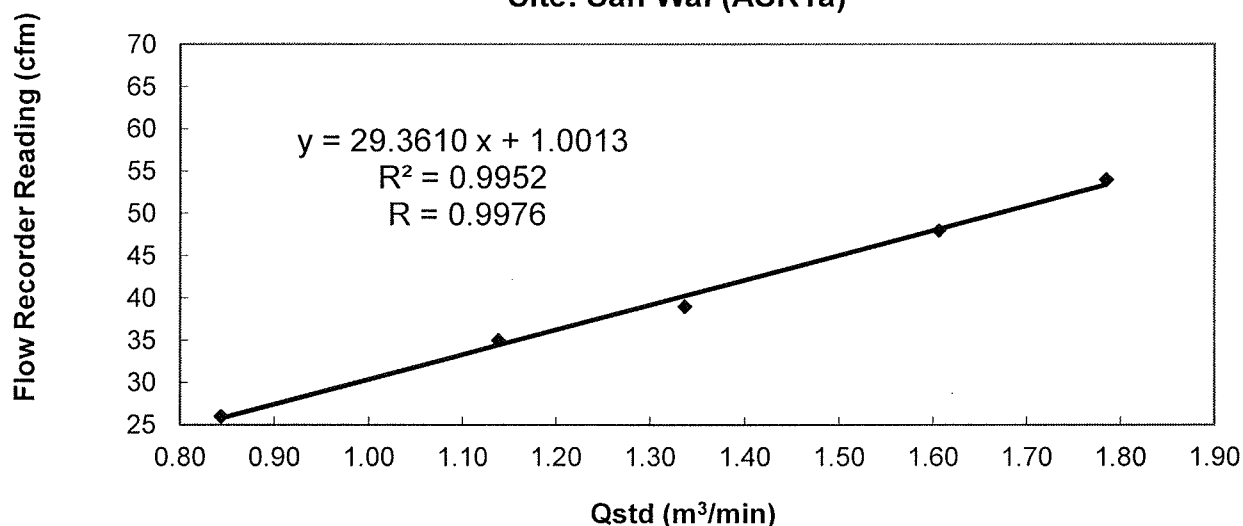

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.


The high volume sampler complies* / does not comply* with the specified requirements and is deemed acceptable* / unacceptable* for use.

Calibrated by :

MAK, Kei Wai
(Assistant Supervisor)

Approved by :

LAU, Chi Leung
(Environmental Team Leader)



Calibration Report
of
High Volume Air Sampler


Manufacturer : Graseby (Model No. GS2310) **Date of Calibration** : 14 February 2019

Serial No. : 9998 (ET / EA / 003 / 12) **Calibration Due Date** : 13 April 2019

Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual


Results :	Flow recorder reading (cfm)	54	48	43	33	29
	Qstd (Actual flow rate, m ³ /min)	1.70	1.53	1.41	1.10	0.92
	Pressure : 767.31 mm Hg	Temp. : 291 K				


Sampler 9998 Calibration Curve
Site: San Wai (ASR2a)

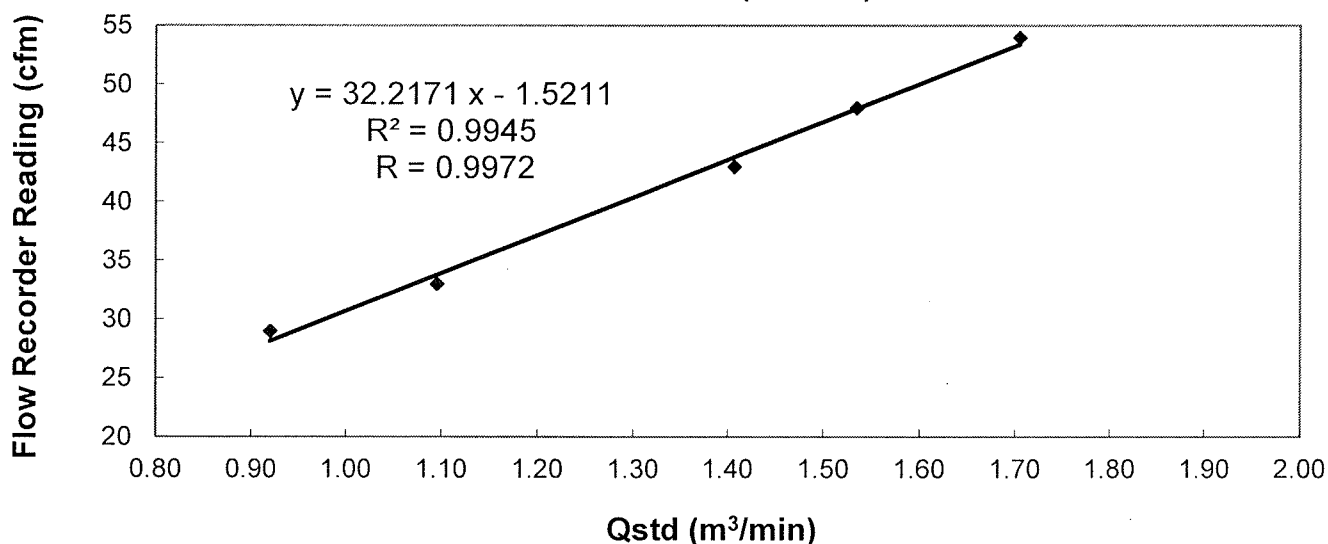


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.

The high volume sampler complies* / ~~does not comply~~* with the specified requirements and is deemed acceptable* / unacceptable* for use.

Calibrated by : 
TANG, Chung Hang
(Supervisor)

Checked by : 
LAU, Chi Leung
(Environmental Team Leader)



Calibration Report
of
High Volume Air Sampler


Manufacturer : Graseby (Model No. GS2310) **Date of Calibration** : 11 April 2019

Serial No. : 9998 (ET / EA / 003 / 12) **Calibration Due Date** : 10 June 2019

Method : Five-point calibration by using standard calibration kit Tisch TE-5025A refer to the Operations Manual

Results :	Flow recorder reading (cfm)	54	47	45	34	29
	Qstd (Actual flow rate, m ³ /min)	1.63	1.47	1.35	1.06	0.87
	Pressure : 767.31 mm Hg	Temp. : 301 K				

Sampler 9998 Calibration Curve
Site: San Wai (ASR2a)

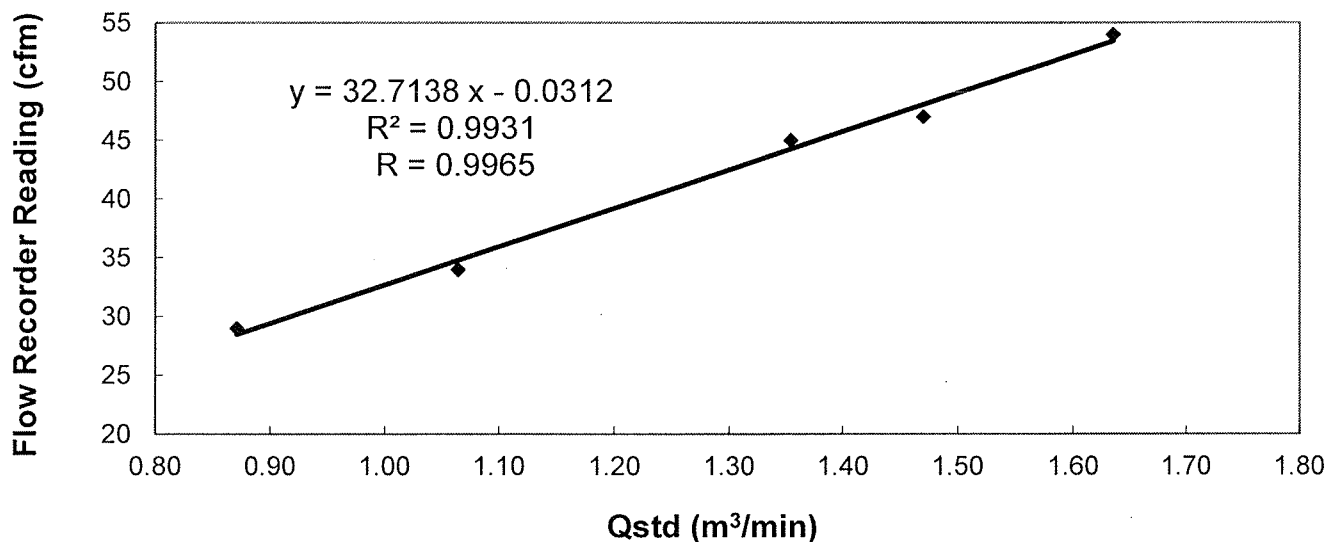

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration.

The high volume sampler complies* / ~~does not comply*~~ with the specified requirements and is deemed acceptable* / unacceptable* for use.

Calibrated by :
MAK, Kei Wai
(Assistant Supervisor)

Checked by :
LAU, Chi Leung
(Environmental Team Leader)

Appendix D2

Impact Air Quality Monitoring Results

Summary of Impact 1-hour TSP Monitoring Results

Air Quality Monitoring Station : ASR1a

Date	Weather	Temperature (°C)	Monitoring Period		1-hr TSP ($\mu\text{g}/\text{m}^3$)
			Start	Finish	
02/04/2019	Fine	20	08:04	09:04	115
02/04/2019	Fine	21	09:04	10:04	66
02/04/2019	Fine	23	10:04	11:04	40
08/04/2019	Fine	25	08:00	09:00	57
08/04/2019	Fine	25	09:00	10:00	40
08/04/2019	Fine	25	10:00	11:00	34
13/04/2019	Cloudy	22	08:24	09:24	85
13/04/2019	Cloudy	22	09:24	10:24	74
13/04/2019	Cloudy	22	10:24	11:24	123
18/04/2019	Fine	28	08:52	09:52	125
18/04/2019	Fine	28	09:52	10:52	118
18/04/2019	Fine	28	10:52	11:52	123
24/04/2019	Fine	27	08:20	09:20	29
24/04/2019	Fine	28	09:20	10:20	29
24/04/2019	Fine	29	10:20	11:20	32
30/04/2019	Fine	20	08:50	09:50	104
30/04/2019	Fine	20	09:50	10:50	107
30/04/2019	Fine	20	10:50	11:50	104
Min					29
Max					125
Average					73

Air Quality Monitoring Station : ASR2b

Date	Weather	Temperature (°C)	Monitoring Period		1-hr TSP ($\mu\text{g}/\text{m}^3$)
			Start	Finish	
02/04/2019	Fine	20	08:09	09:09	49
02/04/2019	Fine	21	09:09	10:09	40
02/04/2019	Fine	23	10:09	11:09	57
08/04/2019	Fine	25	08:08	09:08	60
08/04/2019	Fine	25	09:08	10:08	61
08/04/2019	Fine	25	10:08	11:08	46
13/04/2019	Cloudy	22	08:29	09:29	51
13/04/2019	Cloudy	22	09:29	10:29	76
13/04/2019	Cloudy	22	10:29	11:29	77
18/04/2019	Fine	26	13:10	14:10	109
18/04/2019	Fine	26	14:10	15:10	113
18/04/2019	Fine	26	15:10	16:10	113
24/04/2019	Fine	27	08:26	09:26	33
24/04/2019	Fine	28	09:26	10:26	34
24/04/2019	Fine	29	10:26	11:26	37
30/04/2019	Fine	26	13:20	14:20	116
30/04/2019	Fine	26	14:20	15:20	118
30/04/2019	Fine	26	15:20	16:20	127
Min					33
Max					113
Average					64

Summary of Impact 24-hour TSP Monitoring Results

Air Quality Monitoring Station : ASR1a



Start		Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Paper Weight (g)		Conc. (µg/m ³)	Weather Condition
Date	Time	Date	Time	Initial	Final		Initial	Final		Initial	Final		
02/04/2019	08:08	03/04/2019	08:08	25685.64	25709.64	24	1.1341	1.1341	1.1341	2.7341	2.8313	60	Fine
08/04/2019	08:05	09/04/2019	08:05	25709.64	25733.64	24	1.1341	1.1341	1.1341	2.6588	2.7747	71	Fine
13/04/2019	08:25	14/04/2019	08:25	25733.64	25757.64	24	1.0898	1.0898	1.0898	2.6167	2.7312	73	Cloudy
18/04/2019	08:55	19/04/2019	08:55	25757.64	25781.64	24	1.0558	1.0558	1.0558	2.6771	2.7880	73	Fine
24/04/2019	08:25	25/04/2019	08:25	25781.64	25805.64	24	1.0898	1.0898	1.0898	2.6116	2.7308	76	Fine
30/04/2019	08:55	01/05/2019	08:55	25805.64	25829.64	24	1.0898	1.0898	1.0898	2.6375	2.7379	64	Fine
											Min	60	
											Max	76	
											Average	69	

Air Quality Monitoring Station : ASR2b


Start		Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Paper Weight (g)		Conc. (µg/m ³)	Weather Condition
Date	Time	Date	Time	Initial	Final		Initial	Final		Initial	Final		
02/04/2019	08:15	03/04/2019	08:15	22430.45	22454.45	24	1.0715	1.0715	1.0715	2.6854	2.7813	62	Fine
08/04/2019	08:10	09/04/2019	08:10	22454.45	22478.45	24	1.0715	1.0715	1.0715	2.6943	2.7992	68	Fine
13/04/2019	08:30	14/04/2019	08:30	22478.45	22502.45	24	1.0403	1.0403	1.0403	2.6440	2.7503	71	Cloudy
18/04/2019	13:15	19/04/2019	13:15	22502.45	22526.45	24	1.0097	1.0097	1.0097	2.5488	2.6593	76	Fine
24/04/2019	08:30	25/04/2019	08:30	22526.45	22550.45	24	1.0403	1.0403	1.0403	2.6903	2.8086	79	Fine
30/04/2019	13:25	01/05/2019	13:25	22550.45	22574.45	24	1.0097	1.0097	1.0097	2.6005	2.6877	60	Fine
											Min	60	
											Max	79	
											Average	69	

Appendix D3


Graphical Plots of Impact Air Quality Monitoring Results

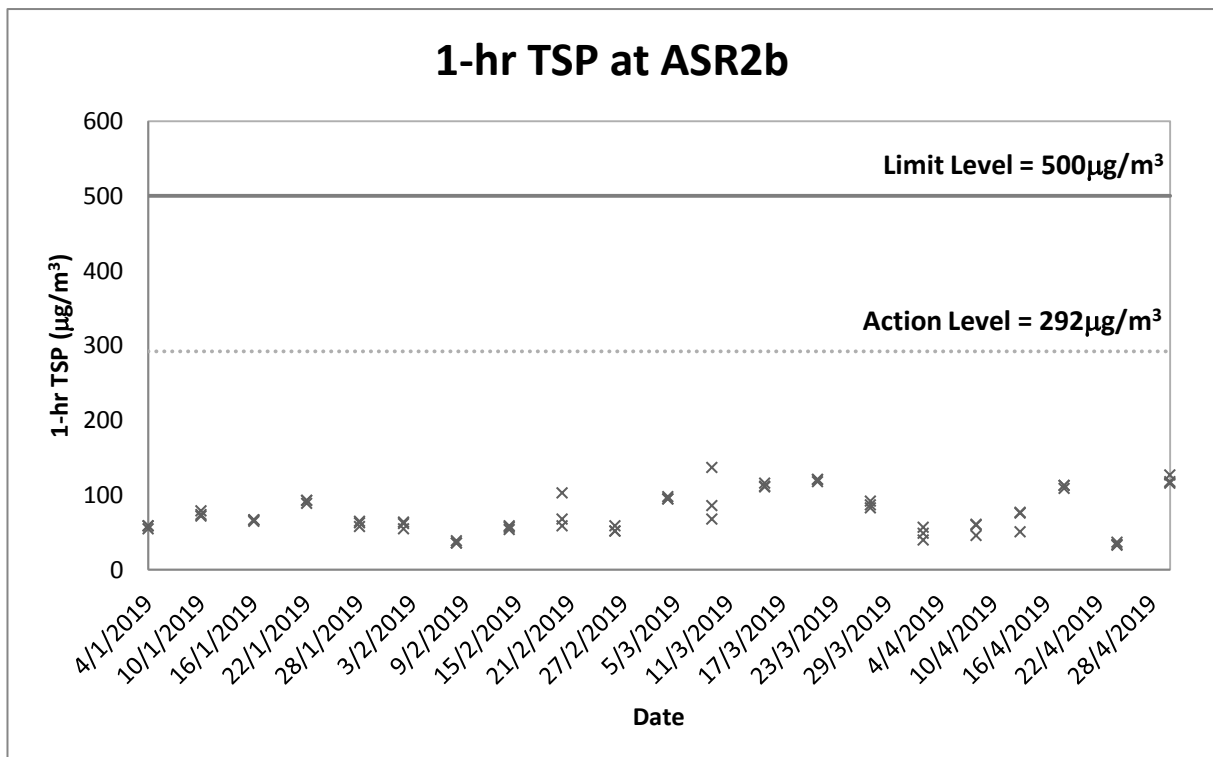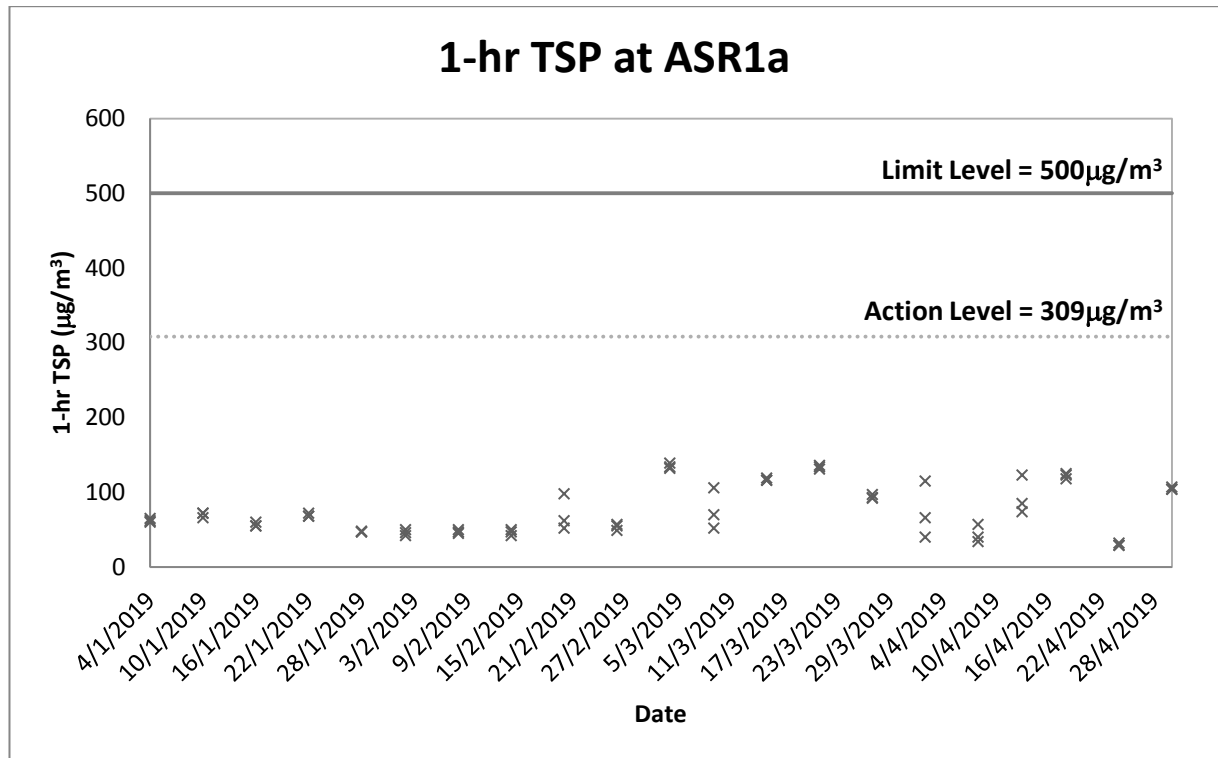

24-hr TSP at ASR1a

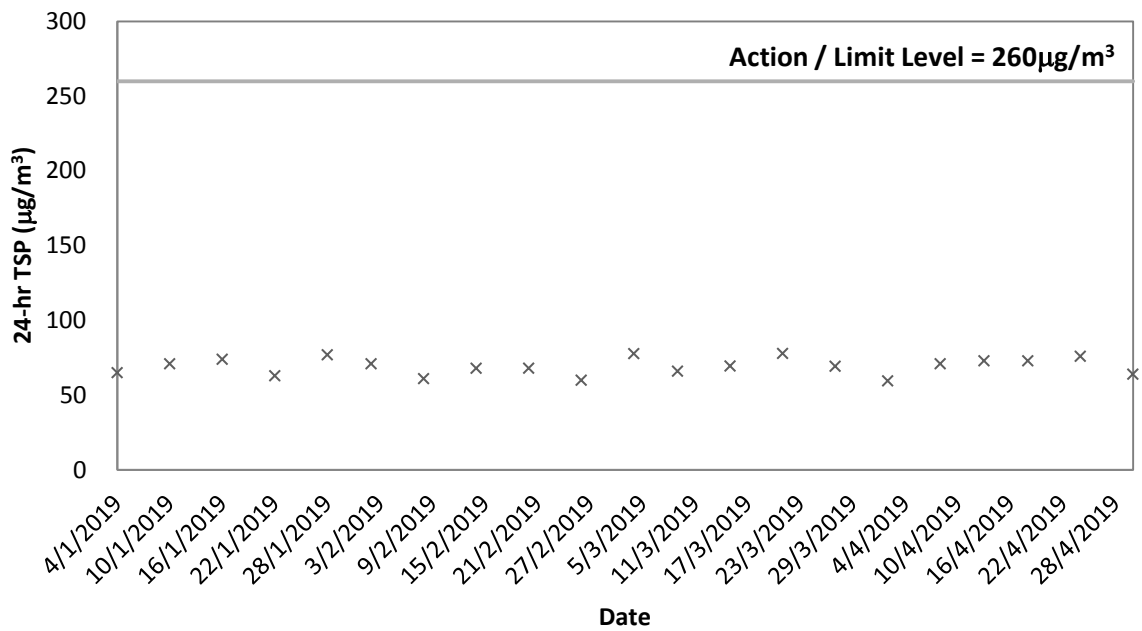

24-hr TSP at ASR2b

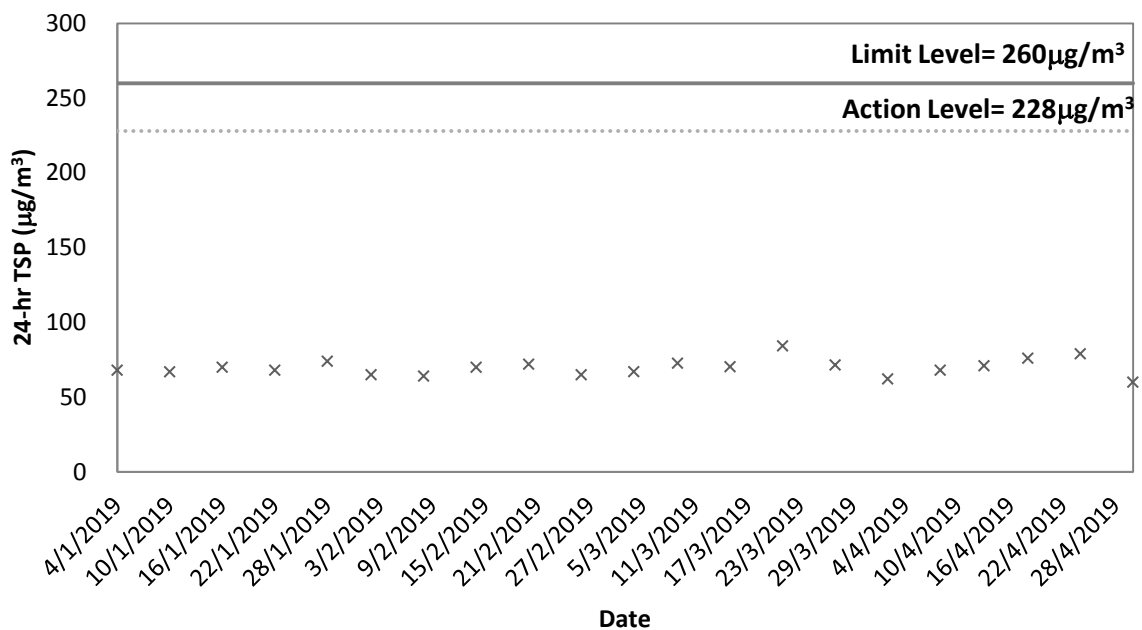

Appendix E1

Calibration Certificates for Impact Noise Monitoring Equipment

Summary of Calibration Certificates for Noise Monitoring Equipment used in this reporting month

Equipment	Equip No.	Serial No.	Calib. Date	Due Date
Sound Level Calibrator (Rion NC-73)	ET/EN/002/01	10196943	23/10/2018	22/10/2019
Sound Level Meter (Rion NL-31)	ET/EN/003/12	00773032	11/12/2018	10/12/2019
Sound Level Meter (Rion NL-52)	ET/EN/003/16	00253765	24/05/2018	23/05/2019
Sound Level Meter (Rion NL-52)	ET/EN/003/18	00264520	27/02/2019	26/02/2020
Sound Level Meter (Rion NL-52)	ET/EN/003/19	00264521	26/03/2019	25/03/2020
Thermo-Anemometer (AZ 8908)	ET/EN/001/05	1064869	04/03/2019	03/03/2020



Calibration Certificate

Certificate No. **810241**

Page **1** of **2** Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q84111

Date of receipt : 15-Oct-18

Item Tested

Description : Sound Level Calibrator

Manufacturer : Rion

I.D. : ET/EN/002/01

Model : NC-73

Serial No. : 10196943

Test Conditions

Date of Test : 23-Oct-18

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure : F21, Z02.

Test Results

All results were within the manufacturer's specification.

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S014	Spectrum Analyzer	805025	NIM-PRC & SCL-HKSAR
S240	Sound Level Calibrator	803357	NIM-PRC & SCL-HKSAR
S041	Universal Counter	802061	SCL-HKSAR
S206	Sound Level Meter	805027	SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by : 

Elva Chong

Approved by : 

Kin Wong

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

Date: 23-Oct-18



Calibration Certificate

Certificate No. 810241

Page 2 of 2 Pages

Results :

1. Level Accuracy (at 1 kHz)

UUT Nominal Value	Measured Value	Mfr's Spec.
94 dB	94.2 dB	± 1 dB

Uncertainty : ± 0.2 dB

2. Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's Spec.
1 kHz	1.017 kHz	± 2 %

Uncertainty : ± 0.1 %

3. Level Stability : 0.0 dB

Uncertainty : ± 0.01 dB


4. Total Harmonic Distortion : < 0.3 %

Mfr's Spec. : < 3 %

Uncertainty : ± 2.3 % of reading

Remarks: 1. UUT : Unit-Under-Test
2. The uncertainty claimed is for a confidence probability of not less than 95%.
3. Atmospheric Pressure : 1 018 hPa

----- END -----



Calibration Certificate

Certificate No. **812029**

Page 1 of 3 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q84795

Date of receipt : 4-Dec-18

Item Tested

Description : Precision Integrating Sound Level Meter

Manufacturer : Rion

I.D. : ET/EN/003/12

Model : NL-31

Serial No. : 00773032

Test Conditions

Date of Test : 11-Dec-18

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure : Z01, IEC 61672.

Test Results

All results were within the IEC 61672 Type 1 or manufacturer's specification

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S017	Multi-Function Generator	C170120	SCL-HKSAR
S240	Sound Level Calibrator	803357	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by :

Elva Chong

Approved by :

Kin Wong

Date: 11-Dec-18


This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full.



Calibration Certificate

Certificate No. 812029

Page 2 of 3 Pages

Results :

1. Self-generated noise: 18.1 dBA (Mfr's Spec ≤ 20 dBA)

2. Acoustical signal test

UUT Setting			Applied Value (dB)	UUT Reading (dB)
Level Range (dB)	Weight	Response		
20 – 100	L _A	Fast	94.0	94.0
		Slow		94.0
	L _C	Fast		94.0
		Fast		94.0
30 – 120	L _A	Fast	94.0	93.9
		Slow		93.9
	L _C	Fast		93.9
		Fast		94.0
30 – 120	L _A	Fast	114.0	113.9
		Slow		113.9
	L _C	Fast		113.9
		Fast		113.9


IEC 61672 Type 1 Spec. : ± 1.1 dB

Uncertainty : ± 0.1 dB

3. Electrical signal tests of frequency weightings (A weighting)

Frequency	Attenuation (dB)	IEC 61672 Type 1 Spec.
31.5 Hz	- 39.7	- 39.4 dB, ± 2 dB
63 Hz	- 26.3	- 26.2 dB, ± 1.5 dB
125 Hz	- 16.3	- 16.1 dB, ± 1.5 dB
250 Hz	- 8.7	- 8.6 dB, ± 1 dB
500 Hz	- 3.3	- 3.2 dB, ± 1.4 dB
1 kHz	0.0 (Ref.)	0 dB, ± 1.1 dB
2 kHz	+ 1.2	+ 1.2 dB, ± 1.6 dB
4 kHz	+ 1.1	+ 1.0 dB, ± 1.6 dB
8 kHz	- 1.2	- 1.1 dB, + 2.1 dB ~ -3.1 dB
16 kHz	- 6.7	- 6.6 dB, + 3.5 dB ~ - 17.0 dB

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 812029

Page 3 of 3 Pages

4. Frequency & Time weightings at 1 kHz

4.1 Frequency Weighting (Fast)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
A	94.0	94.0 (Ref.)	- -	± 0.4 dB
C	94.0	94.0	0.0	
P	94.0	94.0	0.0	

4.2 Time Weighting (A-weighted)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
Fast	94.0	94.0 (Ref.)	- -	± 0.3 dB
Slow	94.0	93.9	-0.1	
Time-averaging	94.0	94.0	0.0	

Uncertainty : ± 0.1 dB

Remarks : 1. UUT : Unit-Under-Test


2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1 007 hPa.

4. Preamplifier model : NH-21 , S/N : 25043

5. The UUT was adjusted with the laboratory's sound calibrator at the reference sound pressure level before the calibration.

----- END -----



Hong Kong Calibration Ltd.

香港校正有限公司

Calibration Certificate

Certificate No. 804850

Page 1 of 3 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q81883

Date of receipt : 15-May-18

Item Tested

Description : Sound Level Meter

Manufacturer : Rion

I.D. : ET/EN/003/16

Model : NL-52

Serial No. : 00253765

Test Conditions

Date of Test : 24-May-18

Supply Voltage : --

Ambient Temperature : (23 ± 3)°C

Relative Humidity : (50 ± 25) %

Test Specifications

Calibration check.

Ref. Document/Procedure: Z01, IEC 61672.

Test Results

All results were within the IEC 61672 Type 1 or manufacturer's specification.

The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S017	Multi-Function Generator	C170120	SCL-HKSAR
S240	Sound Level Calibrator	803357	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by :

Elva Chong

Approved by :

Kin Wong

Date: 24-May-18

This Certificate is issued by:


Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full.

E



Calibration Certificate

Certificate No. 804850

Page 2 of 3 Pages

Results :

1. Self-generated noise: 15.3 dBA (Mfr's Spec ≤ 17 dBA)

2. Acoustical signal test

UUT Setting				Applied Value (dB)	UUT Reading (dB)
Range (dB)	Frequency Weighting	Time Weighting	Octave Filter		
20 ~ 130	A	F	OFF	94.0	94.0
		S	OFF		94.0
	C	F	OFF		94.0
	Z	F	OFF		94.0
	A	F	OFF	114.0	114.0
		S	OFF		114.0
	C	F	OFF		114.0
	Z	F	OFF		114.0

IEC 61672 Type 1 Spec. : ± 1.1 dBUncertainty : ± 0.1 dB

3 Electrical signal tests of frequency weightings (A weighting)

Frequency	Attenuation (dB)	IEC 61672 Type 1 Spec.
31.5 Hz	-39.6	- 39.4 dB, ± 2 dB
63 Hz	-26.2	- 26.2 dB, ± 1.5 dB
125 Hz	-16.2	- 16.1 dB, ± 1.5 dB
250 Hz	-8.7	- 8.6 dB, ± 1 dB
500 Hz	-3.2	- 3.2 dB, ± 1.4 dB
1 kHz	0.0 (Ref)	0 dB, ± 1.1 dB
2 kHz	+1.2	+ 1.2 dB, ± 1.6 dB
4 kHz	+1.0	+ 1.0 dB, ± 1.6 dB
8 kHz	-1.1	- 1.1 dB, + 2.1 dB ~ -3.1 dB
16 kHz	-8.0	- 6.6 dB, + 3.5 dB ~ - 17.0 dB

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 804850

Page 3 of 3 Pages

4. Frequency & Time weightings at 1 kHz

4.1 Frequency Weighting (Fast)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
A	94.0	94.0 (Ref.)	- -	± 0.4 dB
C	94.0	94.0	0.0	
Z	94.0	94.0	0.0	

4.2 Time Weighting (A-weighted)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
Fast	94.0	94.0 (Ref.)	- -	± 0.3 dB
Slow	94.0	94.0	0.0	
Time-averaging	94.0	94.0	0.0	

Uncertainty : ± 0.1 dB

Remarks : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.
3. Atmospheric Pressure : 1 008 hPa.
4. Preamplifier model : NH-25 , S/N : 43795
5. Firmware Version: 1.5
6. Power Supply Check: OK
7. The UUT was adjusted with the laboratory's calibrator at the reference sound pressure level before the calibration.

----- END -----



Calibration Certificate

Certificate No. **901292**

Page **1** of **3** Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q90546

Date of receipt : 14-Feb-19

Item Tested

Description : Sound Level Meter

Manufacturer : Rion

I.D. : ET/EN/003/18

Model : NL-52

Serial No. : 00264520

Test Conditions

Date of Test : 27-Feb-19

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure: Z01, IEC 61672.

Test Results

All results were within the IEC 61672 Type 1 or manufacturer's specification.


The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S017	Multi-Function Generator	C190926	SCL-HKSAR
S240	Sound Level Calibrator	803357	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by : 
Elva Chong

Approved by : 
Kin Wong

Date: 27-Feb-19

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full.



Calibration Certificate

Certificate No. 901292

Page 2 of 3 Pages

Results :

Acoustical signal test

1. Self-generated noise: 15.9 dBA (Mfr's Spec ≤ 17 dBA)

2. Reference Sound Pressure Level

UUT Setting				Applied Value (dB)	UUT Reading (dB)
Range (dB)	Frequency Weighting	Time Weighting	Octave Filter		
20 ~ 130	A	F	OFF	94.0	94.0
		S	OFF		94.0
	C	F	OFF		94.0
	Z	F	OFF		94.0
	A	F	OFF	114.0	114.0
		S	OFF		114.0
	C	F	OFF		114.0
	Z	F	OFF		114.0

IEC 61672 Type 1 Spec. : ± 1.1 dB

Uncertainty : ± 0.1 Db

Electrical signal tests

3. Electrical signal tests of frequency weightings (A weighting)

Frequency	Attenuation (dB)	IEC 61672 Type 1 Spec.
31.5 Hz	-39.6	- 39.4 dB, ± 2 dB
63 Hz	-26.3	- 26.2 dB, ± 1.5 dB
125 Hz	-16.2	- 16.1 dB, ± 1.5 dB
250 Hz	-8.7	- 8.6 dB, ± 1 dB
500 Hz	-3.3	- 3.2 dB, ± 1.4 dB
1 kHz	0.0 (Ref)	0 dB, ± 1.1 dB
2 kHz	+1.2	+ 1.2 dB, ± 1.6 dB
4 kHz	+1.0	+ 1.0 dB, ± 1.6 dB
8 kHz	-1.1	- 1.1 dB, + 2.1 dB ~ -3.1 dB
16 kHz	-8.0	- 6.6 dB, + 3.5 dB ~ - 17.0 dB

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 901292

Page 3 of 3 Pages

4. Frequency & Time weightings at 1 kHz

4.1 Frequency Weighting (Fast)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
A	94.0	94.0 (Ref.)	- -	± 0.4 dB
C	94.0	94.0	0.0	
Z	94.0	94.0	0.0	

4.2 Time Weighting (A-weighted)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
Fast	94.0	94.0 (Ref.)	- -	± 0.3 dB
Slow	94.0	94.0	0.0	
Time-averaging	94.0	94.0	0.0	

Uncertainty : ± 0.1 dB

Remarks : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1 001 hPa.

4. Preamplifier model : NH-25 , S/N : 64645

5. Firmware Version: 1.7

6. Power Supply Check: OK

7. The UUT was adjusted with the laboratory's sound calibrator at the reference sound pressure level before the calibration.

----- END -----



Calibration Certificate

Certificate No. **902820**

Page 1 of 3 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q91096

Date of receipt : 19-Mar-19

Item Tested

Description : Sound Level Meter

Manufacturer : Rion

Model : NL-52

I.D. : ET/EN/003/19

Serial No. : 00264521

Test Conditions

Date of Test : 26-Mar-19

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Supply Voltage : --

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Ref. Document/Procedure: Z01, IEC 61672.

Test Results

All results were within the IEC 61672 Type 1 or manufacturer's specification.


The results are shown in the attached page(s).


Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S017	Multi-Function Generator	C190926	SCL-HKSAR
S240	Sound Level Calibrator	803357	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by : 
Elva Chong

Approved by : 
Kin Wong

Date: 26-Mar-19

This Certificate is issued by:
Hong Kong Calibration Ltd.
Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.
Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full.



Calibration Certificate

Certificate No. 902820

Page 2 of 3 Pages

Results :

Acoustical signal test

1. Self-generated noise: 16.4dBA (Mfr's Spec ≤ 17 dBA)

2. Reference Sound Pressure Level

UUT Setting				Applied Value (dB)	UUT Reading (dB)
Range (dB)	Frequency Weighting	Time Weighting	Octave Filter		
20 ~ 130	A	F	OFF	94.0	94.0
		S	OFF		94.0
	C	F	OFF		94.1
	Z	F	OFF		94.1
	A	F	OFF	114.0	114.1
		S	OFF		114.1
	C	F	OFF		114.1
	Z	F	OFF		114.1

IEC 61672 Type 1 Spec. : ± 1.1 dB


Uncertainty : ± 0.1 Db

Electrical signal tests

3. Electrical signal tests of frequency weightings (A weighting)

Frequency	Attenuation (dB)	IEC 61672 Type 1 Spec.
31.5 Hz	-39.6	- 39.4 dB, ± 2 dB
63 Hz	-26.3	- 26.2 dB, ± 1.5 dB
125 Hz	-16.2	- 16.1 dB, ± 1.5 dB
250 Hz	-8.7	- 8.6 dB, ± 1 dB
500 Hz	-3.3	- 3.2 dB, ± 1.4 dB
1 kHz	0.0 (Ref)	0 dB, ± 1.1 dB
2 kHz	+1.2	+ 1.2 dB, ± 1.6 dB
4 kHz	+1.0	+ 1.0 dB, ± 1.6 dB
8 kHz	-1.1	- 1.1 dB, + 2.1 dB ~ -3.1 dB
16 kHz	-8.0	- 6.6 dB, + 3.5 dB ~ - 17.0 dB

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 902820

Page 3 of 3 Pages

4. Frequency & Time weightings at 1 kHz

4.1 Frequency Weighting (Fast)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
A	94.0	94.0 (Ref.)	- -	± 0.4 dB
C	94.0	94.0	0.0	
Z	94.0	94.0	0.0	

4.2 Time Weighting (A-weighted)

UUT Setting	Applied Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
Fast	94.0	94.0 (Ref.)	- -	± 0.3 dB
Slow	94.0	94.0	0.0	
Time-averaging	94.0	94.0	0.0	

Uncertainty : ± 0.1 dB

Remarks : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 1 008 hPa.

4. Preamplifier model : NH-25 , S/N : 64646

5. Firmware Version: 1.7

6. Power Supply Check: OK

7. The UUT was adjusted with the laboratory's sound calibrator at the reference sound pressure level before the calibration.

----- END -----



Calibration Certificate

Certificate No. **901843**

Page 1 of 2 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q90738

Date of receipt : 26-Feb-19

Item Tested

Description : Thermo-Anemometer

Manufacturer : AZ Instrument

Model : AZ 8908

I.D. : ET/EN/001/05

Serial No. : 1064869

Test Conditions

Date of Test : 4-Mar-19

Supply Voltage : --

Ambient Temperature : $(23 \pm 3)^{\circ}\text{C}$

Relative Humidity : $(50 \pm 25) \%$

Test Specifications

Calibration check.

Calibration procedure : T03, Z04.

Test Results

A correction factor of x 1.1 is required to bring the meter reading to within the manufacturer's specification.
The results are shown in the attached page(s).

Main Test equipment used:

<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Traceable to</u>
S155	Std. Anemometer	809939	NIM-PRC
S223C	Std. Thermometer	805692	NIM-PRC

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI), or by reference to a natural constant.
The test results apply to the above Unit-Under-Test only

Calibrated by : PN Lee

Approved by : Steve Kwan

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646

Date: 4-Mar-19



Calibration Certificate

Certificate No. **901843**

Page 2 of 2 Pages

Results :

1. Velocity

Applied Value (m/s)	UUT Reading (m/s)	Corrected Reading (UUT Rdg. \times 1.1)	Mfr's Spec.
0.00	0.0	0.0	\pm (3 % of reading + 0.2 m/s)
2.50	2.3	2.5	
5.00	* 4.6	5.1	
10.00	* 9.0	9.9	
15.00	* 13.6	15.0	
19.00	* 17.0	18.7	

2. Temperature

Applied Value (°C)	UUT Reading (°C)	Mfr's Spec.
23.49	23.2	\pm 1 °C

Remark : 1. UUT: Unit-Under-Test

2. Uncertainty : \pm (0.9 % + 0.16 m/s) for Velocity, \pm 0.1 °C for Temperature, for a confidence probability of not less than 95 %.

3. Atmospheric Pressure : 1 001 hPa

4. * Out of Specification.

----- END -----

Appendix E2

Impact Noise Monitoring Results

Day-time Noise Monitoring

Monitoring Station: NSR1a

Date	Weather	Temperature (°C)	Start Time (hh:mm)	End Time (hh:mm)	Noise Level at NSR1a, dB (A)			Wind Speed (m/s)
					Leq (30min)	L10 (30min)	L90 (30min)	
02/04/19	Fine	20	08:52	09:22	67.3	69.3	59.9	0.2
08/04/19	Fine	25	08:48	09:18	66.6	68.5	58.5	0.2
13/04/19	Cloudy	22	09:09	09:39	68.3	69.1	61.2	0.6
18/04/19	Fine	28	08:54	09:24	67.5	70.4	65.1	0.3
24/04/19	Fine	27	09:06	09:36	66.5	67.0	61.4	0.5
30/04/19	Fine	20	08:50	09:20	63.1	67.4	59.4	0.2
Min					63.1	67.0	58.5	
Max					68.3	70.4	65.1	
Logarithmic Average for normal weekdays					66.8	68.8	61.5	

Monitoring Station: NSR2b


Date	Weather	Temperature (°C)	Start Time (hh:mm)	End Time (hh:mm)	Noise Level at NSR2b, dB (A)			Wind Speed (m/s)
					Leq (30min)	L10 (30min)	L90 (30min)	
02/04/19	Fine	20	08:09	08:39	58.9	61.3	55.8	0.2
08/04/19	Fine	25	08:08	08:38	63.1	64.4	58.6	0.2
13/04/19	Cloudy	22	08:29	08:59	66.9	68.5	62.3	0.4
18/04/19	Fine	28	13:11	13:41	66.4	69.8	63.2	0.2
24/04/19	Fine	27	08:26	08:56	64.7	66.4	62.6	0.2
30/04/19	Fine	20	13:20	13:50	67.2	70.5	63.4	0.1
Min					58.9	61.3	55.8	
Max					67.2	70.5	63.4	
Logarithmic Average for normal weekdays					65.3	67.8	61.7	

(*) : 3dB(A) correction was added to the results during the free-field noise measurements


Appendix E3

Graphical Plots of Impact Noise Monitoring Data

Noise Level at NSR1a

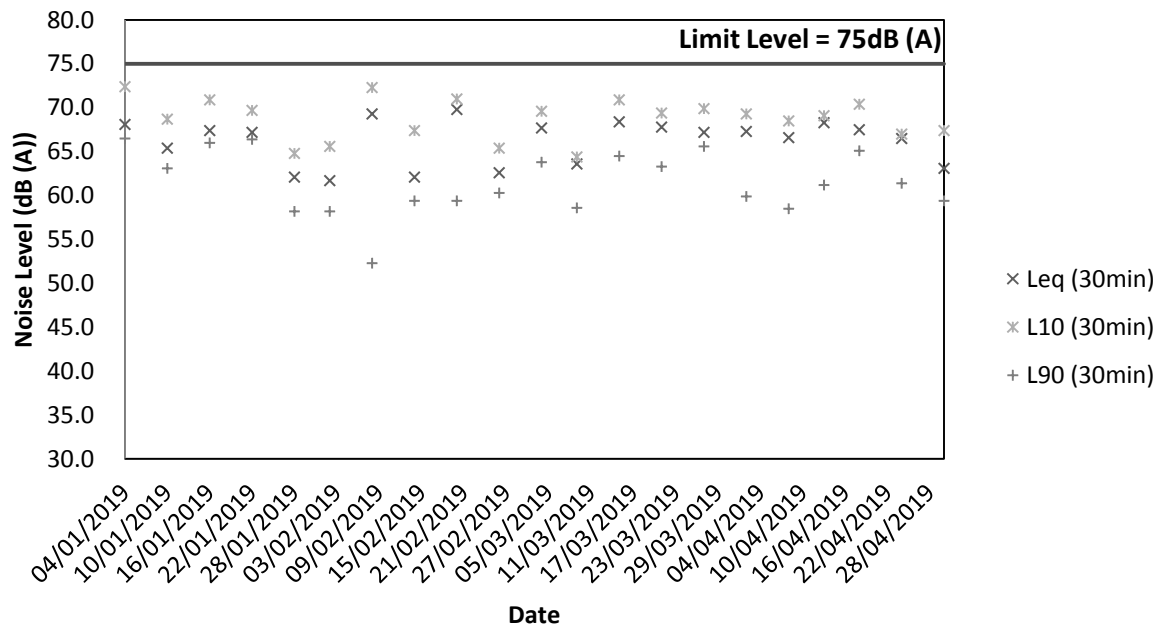

Noise Level at NSR2b

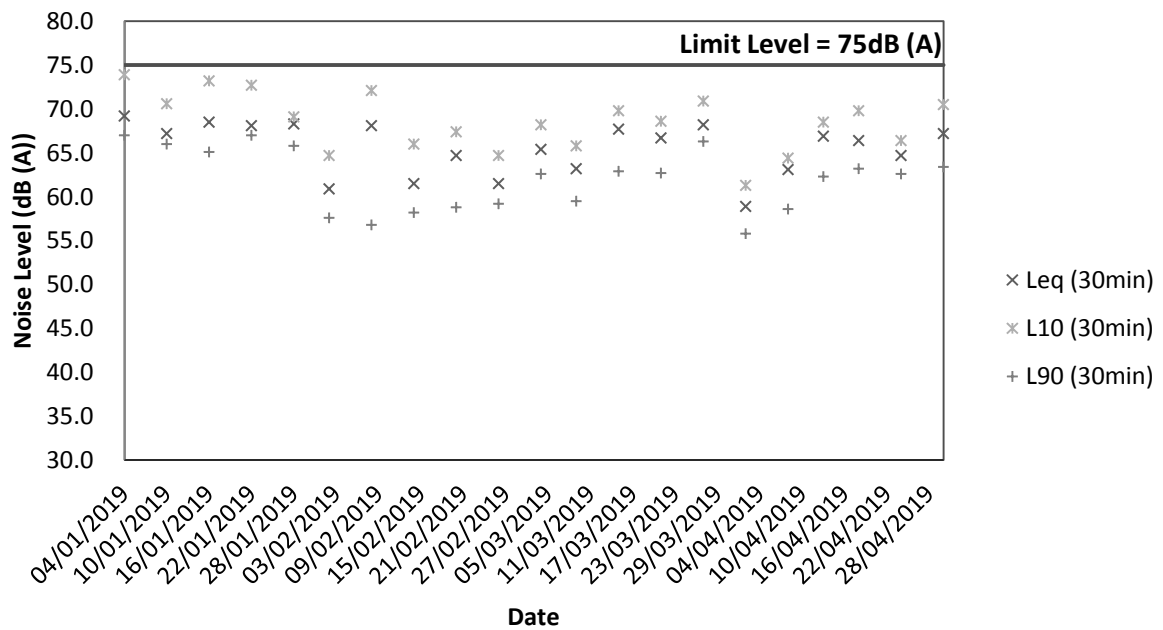

Appendix F1

Calibration Certificates for Impact Water Quality Monitoring Equipments



Calibration Report of Dissolved Oxygen Meter (*In situ* Measurement)

Equipment Ref. No. : ET/EW/008/006 Manufacturer : YSI
Model No. : Pro 2030 Serial No. : 12A100554
Calibration Date : 2/3/2019 Calibration Due Date : 1/6/2019

Temperature Verification by Reference Thermometer (ET/0521/028)

	Temperature Reading (°C)	Correction (°C)	Corrected Temperature (°C)	Difference (°C)
Reference Thermometer	20.2	0.0	20.2	0.1
DO Meter	20.3	0.0	20.3	

Criteria: Difference between corrected temperature from DO meter and reference thermometer : $< \pm 0.5^{\circ}\text{C}$

Zero Point Checking

DO meter reading (mg/L)	0.01
-------------------------	------

Criteria: Zero checking: 0.0 mg/L

Linearity Checking of Dissolved Oxygen Content by APHA 19ed 4500-O G

Purging time, min	Expected DO value (mg/L) (ET/0510/012)	DO meter reading (mg/L)	Difference of DO Content (mg/L)
2	6.22	6.41	0.19
5	3.88	3.96	0.08
10	2.15	2.31	0.16

Criteria: Difference between DO meter reading and expected DO value: $< \pm 0.30\text{ mg/L}$

Salinity Checking by APHA 19ed 2520 B

	Expected Salinity (ppt)	DO meter reading (ppt)
Reagent No. of NaCl (10 ppt): CPE/012/4.7/27	10	9.3
Reagent No. of NaCl (30 ppt): CPE/012/4.8/27	30	28.5

Criteria: Difference between DO meter reading and expected Salinity: $\pm 10.0\%$

The equipment complies [#] / ~~does not comply~~ [#] with the specified requirements and is deemed acceptable [#] / unacceptable [#] for use.

[#] Delete as appropriate

Calibrated by : 

Approved by : 



Performance Check of Turbidity Meter

Equipment Ref. No. : ET/0505/021 Manufacturer : HACH
Model No. : 2100Q Serial No. : 17020C056013
Date of Calibration : 25/1/2019 Due Date : 24/4/19

Theoretical Value of Turbidity Standard (NTU)	Measured Value (NTU)	Difference % *
20	20.6	3.0%
100	101	1.0%
800	791	-1.1%

(*) Difference = (Measured Value – Theoretical Value) / Theoretical Value x 100

Acceptance Criteria

Difference : -5 % to 5 %

The turbidity meter complies * / ~~does not comply~~ * with the specified requirements and is deemed acceptable * / ~~unacceptable~~ * for use. Measurements are traceable to national standards.

Prepared by :  Checked by : 



Performance Check of Turbidity Meter

Equipment Ref. No. : ET/0505/021 Manufacturer : HACH
Model No. : 2100Q Serial No. : 17020C056013
Date of Calibration : 25/4/2019 Due Date : 24/7/19


Theoretical Value of Turbidity Standard (NTU)	Measured Value (NTU)	Difference % *
20	20.2	1.0%
100	102	2.0%
800	785	-1.9%


(*) Difference = (Measured Value – Theoretical Value) / Theoretical Value x 100

Acceptance Criteria

Difference : -5 % to 5 %

The turbidity meter complies * / ~~does not comply~~ * with the specified requirements and is deemed acceptable * / ~~unacceptable~~ * for use. Measurements are traceable to national standards.

Prepared by : 

Checked by : 

Appendix F2

Impact Water Quality Monitoring Results

Impact Water Quality Monitoring

Monitoring Station: R1b

Date	Sampling Duration	Weather Condition	Sampling Level	Turbidity (NTU)			Dissolved Oxygen (DO) (mg/L)			Suspended Solid (SS) (mg/L)		
				1	2	Ave.	1	2	Ave.	1	2	Ave.
02/04/19	15:18-15:27	Cloudy	Mid-Depth	7.1	7.2	7.2	2.23	2.18	2.21	<5	<5	<5
04/04/19	13:24-13:33	Cloudy	Mid-Depth	10.1	10.2	10.2	2.13	2.10	2.12	<5	<5	<5
06/04/19	09:30-09:35	Fine	Mid-Depth	4.3	4.3	4.3	2.27	2.30	2.29	<5	<5	<5
09/04/19	14:50-14:55	Cloudy	Mid-Depth	9.5	9.5	9.5	2.06	2.09	2.08	<5	<5	<5
11/04/19	12:50-12:55	Cloudy	Mid-Depth	9.0	9.1	9.1	2.30	2.34	2.32	5	<5	<5
13/04/19	08:35-08:40	Cloudy	Mid-Depth	12.4	12.6	12.5	2.87	2.85	2.86	5	5	5
16/04/19	13:32-13:40	Cloudy	Mid-Depth	15.8	15.7	15.8	1.96	1.99	1.98	9	9	9
18/04/19	13:40-13:51	Cloudy	Mid-Depth	8.8	8.7	8.7	2.18	2.14	2.16	<5	<5	<5
20/04/19	09:30-10:00	Cloudy	Mid-Depth	3.9	4.0	4.0	1.88	1.91	1.90	<5	<5	<5
23/04/19	15:08-15:17	Cloudy	Mid-Depth	4.2	4.1	4.2	2.95	2.92	2.94	<5	<5	<5
25/04/19	14:10-14:19	Cloudy	Mid-Depth	6.7	6.8	6.7	2.47	2.43	2.45	<5	<5	<5
27/04/19	13:15-13:24	Cloudy	Mid-Depth	7.1	7.0	7.0	2.27	2.25	2.26	<5	<5	<5
30/04/19	13:48-13:57	Cloudy	Mid-Depth	9.2	9.1	9.2	2.15	2.11	2.13	<5	<5	<5
				Min		3.9	Min		1.88	Min		<5
				Max		15.8	Max		2.95	Max		9
				Average		8.2	Average		2.29	Average		1


Remark(s):

- (#) 200ml sample was used for Suspended Solids analysis. Practical Quantitation Limit of Suspended Solids reported less than 5 mg/L. The results reported as <5 would be counted as zero for average measurement.


Appendix F3

Graphical Plots of Impact Water Quality Monitoring Data


Impact Turbidity Result

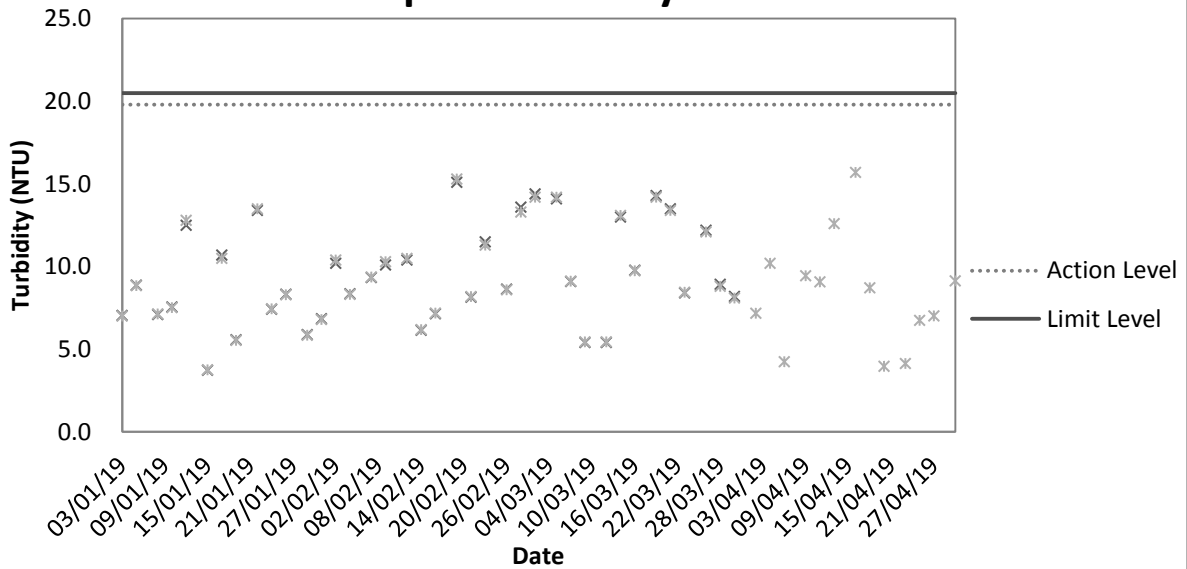

Impact DO Result

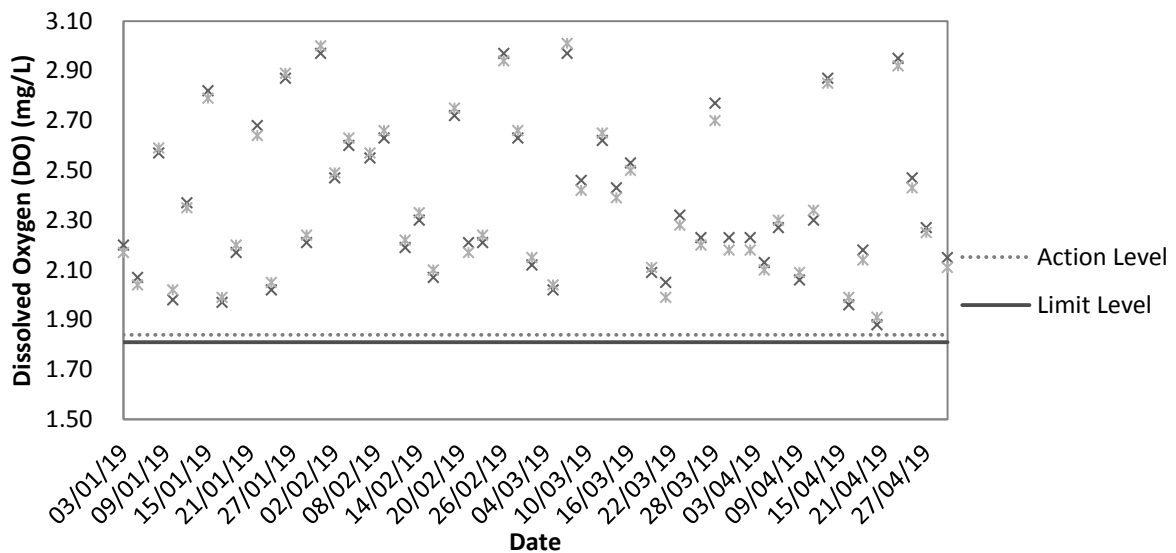

Impact Suspended Solid (SS) Result

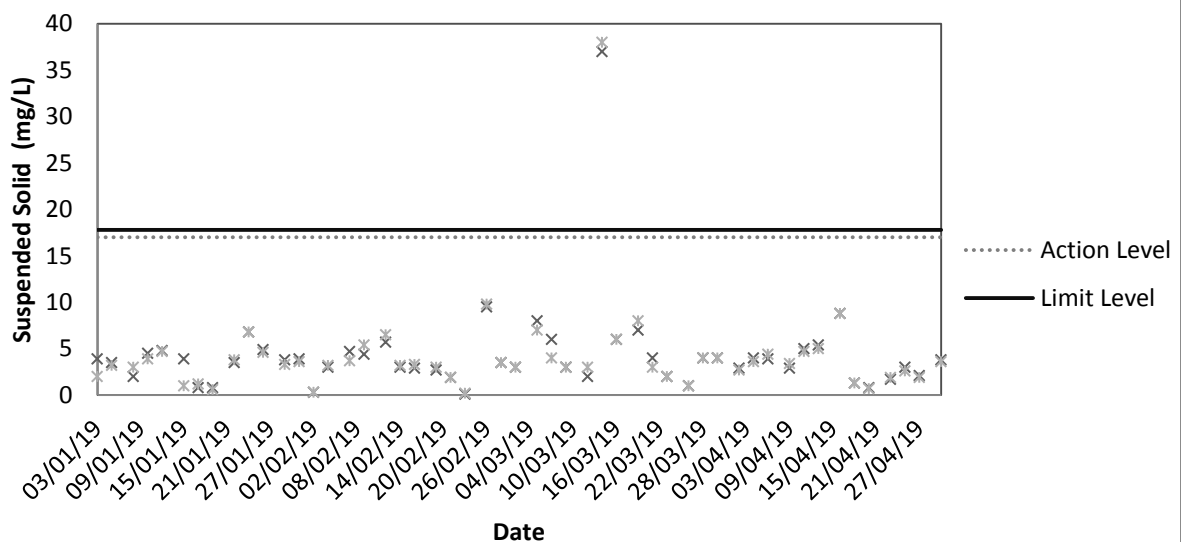

Appendix G

Weather Condition



Daily Extract of Meteorological Observations, April 2019

Day	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Total Rainfall (mm)	Prevailing Wind Direction (degrees)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)				
01	1019.3	21.6	20.3	19.7	16.8	81	91	Trace
02	1018.2	23.0	20.7	18.9	16.3	76	89	Trace
03	1016.9	25.7	22.8	20.7	19.0	80	85	Trace
04	1016.7	23.8	21.7	20.4	18.6	83	86	Trace
05	1014.5	27.4	24.0	20.9	19.5	76	37	0.0
06	1013.0	28.1	25.1	22.4	21.0	79	27	0.0
07	1012.5	28.0	25.7	23.7	21.9	80	48	0.0
08	1011.6	29.9	26.7	25.1	23.0	80	80	0.0
09	1011.1	28.9	26.6	25.5	23.1	81	79	0.0
10	1010.9	30.1	27.1	25.3	23.2	80	79	0.0
11	1010.0	29.9	27.3	25.3	23.7	81	84	0.7
12	1013.3	25.2	22.3	21.0	20.3	89	91	6.1
13	1014.3	22.3	21.2	20.3	19.9	92	98	3.8
14	1013.8	24.4	22.7	21.9	20.9	90	92	10.4
15	1014.4	23.1	22.1	20.9	19.4	85	91	1.1
16	1012.6	23.6	21.2	19.5	19.6	91	87	9.2
17	1012.2	26.1	23.5	21.5	20.7	85	77	0.0
18	1010.0	25.0	24.0	23.0	22.1	90	91	6.7
19	1007.7	28.6	23.7	21.3	22.3	93	90	75.8
20	1007.2	26.2	23.3	21.9	22.5	95	93	43.6
21	1008.0	30.1	26.2	23.2	24.0	88	81	0.3
22	1009.3	30.1	27.5	25.6	24.5	84	72	0.0
23	1010.4	31.0	28.0	26.0	24.3	81	58	0.0
24	1009.9	31.2	28.0	26.2	23.7	78	57	0.0
25	1009.3	31.1	28.5	26.4	24.0	77	39	0.0
26	1010.4	31.5	28.4	26.2	24.7	81	58	0.9
27	1012.8	26.4	24.9	22.3	22.4	86	91	16.6
28	1013.2	26.9	24.3	22.7	22.4	89	85	3.1
29	1010.9	29.2	26.4	24.7	23.8	86	71	0.0
30	1008.0	28.8	26.7	25.3	23.3	82	83	7.5
Mean/Total	1012.1	27.2	24.7	22.9	21.7	84	76	185.8
Normal [§]	1012.9	25.0	22.6	20.8	19.4	83	81	174.7

Remark(s):

- Trace means rainfall less than 0.05 mm
- § 1981-2010 Climatological Normal
- The meteorological observations extracted from Hong Kong Observatory only shown the daily average and may be varied from the weather condition recorded during monitoring.

Appendix H

Environmental Site Inspection Checklist



Environmental Site Inspection Checklist – San Wai

Inspection Date: 04 April 2018 Inspected By: C. L. Lau
Time: 15:00 Weather Condition: Fine
Participants: Patrick Leung, Teddy Yuen, Abby Sham, Jason Leung

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <u>Not observed</u>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding ≥ 2.4 m tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	Construction Activities				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Item 1
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit: *Follow up action to items on 29/03/2018, all items were improved.*

Observations *Item 1 : General refuse was observed.*

Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

To collect the general refuse properly.

Signature:

ET's representative

Name: *C. L. Lau*

Date: *04/04/2018*

Signature:

Contractor's representative

Name: *Abby Sham*

Date: *4/4/2018*

Signature:

ET Leader

Name: *C. L. Lau*

Date: *04/04/2018*



Signature:


SO's representative

Name: *C. F. Wong*

Date: *04/04/2018*

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 29/03/2019, chemical container was removed.</p>	--	190404_001	No	--
--	 <p>Follow up action to Item 2 on 29/03/2019, general refuse and C&D wastes were collected.</p>	--	190404_002	No	--

1	 <p>General refuse was observed.</p>	To collect the general refuse properly	190404_003	Yes	12/04/2019
---	--	--	------------	-----	------------

Environmental Site Inspection Checklist – San Wai

Inspection Date:

12.4.19

Inspected By:

Frankie Tang

Time:

9.00

Weather Condition:

Fine

Participants:

Patrick Lenny, Teddy Yuen, Abby Sham, Jackson Lenny

1	Permits/Licenses	N/A	Yes	No	Remarks
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality	N/A	Yes	No	Remarks
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input type="checkbox"/> Others:				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding \geq 2.4m tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

Follow up actions for pervious Site Audit: Follow up action to all item on 4.4.19,
all item was improved.

Observations

No observation was recorded on this site inspection

Corrective Actions – Mitigation Measures Implemented or Proposed (if any): NA

Signature:
ET's representative



Name: Frankie Tse

Date: 12.4.19

Signature:
Contractor's representative



Name: Abby Sham

Date: 12/4/19


Signature:
ET Leader



Name: C.L. Lau

Date: 13/04/2019


Signature:
SO's representative



Name: Jaanw

Date: 12/4/2019

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 04/04/2019, general refuse were collected.</p>	--	190412_001	No	--

Environmental Site Inspection Checklist – San Wai

Inspection Date: 18.4.19 Inspected By: Frankie Tin
Time: 10:00 Weather Condition: Fine
Participants: Patrick Leung, Teddy Yuen, Abby Sun, Joshua Leung

		N/A	Yes	No	Remarks
1	Permits/Licenses				
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality				
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <u>Not observed</u>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding $\geq 2.4\text{m}$ tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	item 1
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	1/2
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	


Follow up actions for pervious Site Audit: *NA*

Observations *Item 1: Fill material was found without cover at UV Zone*
Item 2: Stagnant water was observed at SDB Zone


Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

Item 1: Provide the cover for fill material properly
Item 2: To clean the stagnant water properly


Signature:
ET's representative


Name: *Paulie Tung*
Date: *18.4.19*


Signature:
Contractor's representative


Name: *Abby Sham*
Date: *18/4/19*

Signature:
ET Leader


Name: *C.L. Lau*
Date: *23/04/2019*

Signature:
SO's representative


Name: *c718026*
Date: *18/6/19*

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
1	 <p>Fill material was found without cover at UV Zone.</p>	To cover the fill material properly	190418_001	Yes	26/04/2019
2	 <p>Stagnant water was observed at SDB Zone.</p>	To clear the stagnant water properly	190418_002	Yes	26/04/2019

Environmental Site Inspection Checklist – San WaiInspection Date: 26.4.19Inspected By: Frankie TangTime: 14:00Weather Condition: FineParticipants: Patrick Leung, Teddy Yuen, Alvin Shum, Jackson Leung

		N/A	Yes	No	Remarks
1	Permits/Licenses				
1.1	Are Environmental Permit, license/ other permit displayed at major site exit and vehicle access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.2	Are Construction Noise Permits available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.3	Is wastewater discharge license available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.4	Are trip tickets for chemical waste and construction waste disposal available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
1.5	Are relevant license/permits for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2	Air Quality				
2.1	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.2	Are speed controlled at 10 km/h on unpaved site areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.3	Are plant and equipment well maintained (i.e. without black smoke from powered plant)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.4	Observed dust source(s): <input type="checkbox"/> Wind erosion <input type="checkbox"/> Vehicle/ Equipment Movements <input type="checkbox"/> Loading/ unloading of materials <input checked="" type="checkbox"/> Others: <u>Not observed</u>				
2.5	Are the work sites wetted with water twice a day?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.6	After removal of boulders, poles, pillars or temporary or permanent structures, are the entire surface sprayed with water or a dust suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.7	Is the area involved demolished items covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.8	Are wheel washing facilities with high pressure water jet provided at all site exits if practicable?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.9	Are the areas of washing facilities and the road section between the washing facilities and the exit point paved with concrete, bituminous materials or hardcores?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.10	Are hoarding $\geq 2.4\text{m}$ tall provided beside roads or area with public access?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.11	Are main haul road paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.12	Are construction site that is within 30m of a discernible or designated vehicle entrance or exit kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.13	Are all vehicles and plant cleaned before they leave the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.14	Are loaded dump trucks covered by impervious sheeting appropriately	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



	before leaving the site?				
2.15	Are working areas of any excavation or earth moving operation sprayed with water or a dusty suppression chemical immediately?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.16	Is exposed earth properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, concrete or other suitable surface stabilizer within 6 months after the last construction activity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.17	Are stockpile of dusty material covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or dust suppression chemical?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.18	Are unpaved areas / designated roads watered regularly to avoid dust generation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
2.19	Are dusty materials covered entirely by impervious sheeting or sprayed with water?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.20	Is every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) covered entirely by impervious sheeting or placed in an area sheltered on the top and 3 sides?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.21	Are the approval or exempted NRMM labels painted or securely fixed on site machines or vehicles and displayed at a conspicuous position according to the Air Pollution Control (Non-road Mobile Machinery) (Emission) Regulation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	

3	Noise	N/A	Yes	No	Remarks
3.1	Are idle plant/equipments turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.2	Are silenced equipments or quiet plants utilized?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.3	Are the silencers or mufflers properly fitted on construction equipments and maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.4	Is temporary hoarding installed located on the site boundaries between noisy construction activities and NSRs?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.5	Are noise barriers (typically density @14kg/m ²) acoustic mat or full enclosure close to noise plants including air compressor, generators and saw etc. provided to protect NSRs?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
3.6	Do air compressors have valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.7	Are compressor operated with doors closed?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.8	QPME used with valid noise labels?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.9	Are construction activities planned so that parallel operation of several sets of equipment close to a given receiver is avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Major noise source(s): <input type="checkbox"/> Traffic <input checked="" type="checkbox"/> Construction activities inside of site <input type="checkbox"/> Construction activities outside of site <input type="checkbox"/> Others:				

4	Water Quality	N/A	Yes	No	Remarks
	<u>Construction Activities</u>				
4.1	Before a rainstorm, are exposed stockpiles covered with tarpaulin or impervious sheets?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.2	Are stockpiles of materials placed in the locations away from the drainage channel?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	



4.3	Are site drainage systems and treatment facilities provided to minimize the water pollution?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.4	Is the treated effluent quality met the requirements specified in the discharge license?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.5	Is the sewage generated from toilets collected using a temporary storage system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.6	Are sewage effluent and discharges from on-site kitchen facilities directed to public foul sewers or collected in a temporary storage tank if connection to public foul sewers is not feasible?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.7	Is a licensed waste collector employed to clean the chemical toilets and temporary storage tank on a regular basis?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.8	Is the storm drainage directed to storm drains via adequately designed sand/ silt removal facilities e.g. sand traps, silt traps and sediment basins?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.9	Are measures taken to prevent the washout of construction materials, soil, silt or debris into any drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.10	Are manholes adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and prevent storm run-off getting into foul sewers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Is a wheel washing bay provided at every site exit?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.12	Is the wheel wash overflow directed to silt removal facilities before being discharged to the storm drain?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.13	Is the section of construction road between the wheel washing bay and the public road surfaced with crushed stone or coarse gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
4.14	Does the surface runoff from bunded areas pass through oil/grease traps prior to discharge to the storm water system?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are sedimentation tanks or package treatment systems provided to treat the large amount of sediment-laden wastewater generated from wheel washing, site runoff and construction works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5	Waste / Chemical Management	N/A	Yes	No	Remarks
	<u>General Waste</u>				
5.1	Are sufficient waste disposal points provided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.2	Is waste disposed regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.3	Is the general waste generated on-site stored in enclosed bins or compaction units separately from the construction and chemical wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.4	Are separated labeled containers/ areas provided for facilitating recycling and waste segregation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
	<u>Construction Waste</u>				
5.5	Are the temporary stockpiles maintained regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.6	Are the C&D materials sorted and recycled on-site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.7	Are the public fill and C&D waste segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.8	Is the segregation and storage of C&D wastes undertaken in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



5.9	Are waste storage area properly cleaned and do not cause windblown litter and dust nuisance?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.10	Are surplus inert C&D materials only consist of earth, building debris and broken rock and concrete and free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered unsuitable by the public filling supervisor?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical / Fuel Storage Area</u>					
5.11	Are the fuel tanks and chemical storage areas provided with locks and sited on sealed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.12	Are the storage areas labeled and separated (if needed)?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.13	Do the storage areas have adequate ventilation and be covered to prevent rainfall entering?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.14	Are the containers used for the storage of chemical wastes suitable for the substance that are holding, resist to corrosion, maintained in a good condition, and securely closed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.15	Are proper measures to control oil spillage during maintenance or to control other chemicals spillage? (e.g. provide drip trays)	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Chemical Waste / Waste Oil</u>					
5.16	Is chemical waste or waste oil stored and labeled in English and Chinese properly in designated area?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.17	Are chemicals and waste oil collected and stored for recycling or proper disposal?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
<u>Records</u>					
5.18	Is a licensed waste hauler used for waste collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.19	Are the records of quantities of wastes generated, recycled and disposed properly kept?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
5.20	For the demolition material/ waste, is the number of loads for each day recorded as appropriate?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6	Landscape and Visual Impacts	N/A	Yes	No	Remarks
6.1	Is the work site confined within site boundaries?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
6.2	Is damage to surrounding areas avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
7	Environmental Complaint	N/A	Yes	No	Remarks
7.1	Number of Environmental Complaint received from dd/mm/yyyy to dd/mm/yyyy?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
8	General Housekeeping	N/A	Yes	No	Remarks
8.1	Are potential stagnant pools cleared and mosquito breeding prevented?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Item 2
8.2	Are the defined boundaries of working areas identified to prevent loss of vegetation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
9	Others	N/A	Yes	No	Remarks
9.1	Are the portable toilets maintained in a state, which will not deter the workers from utilizing these portable toilets?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	



Follow up actions for pervious Site Audit: Follow up action to item on 18.4.19, all item was improved.

Observations

Item 1: Stagnant water was accumulated on the ^{drain} trips at PL Zone

Corrective Actions – Mitigation Measures Implemented or Proposed (if any):

Item 1: To clean the stagnant water properly.

Signature:

ET's representative

Name: Frankie Tse

Date: 26-4-19

Signature:

Contractor's representative

Name: Abby Sham

Date: 26/4/19

Signature:

ET Leader

Name: C.L. Lau

Date: 27/04/2019



Signature:


SO's representative

Name: C.F. Chow

Date: 26/4/2019

Summary of the Weekly Environmental Site Inspection

Item	Details of observations	Follow Up Action	Photo Ref.	Further Action Required (Yes/No)	Proposed Follow up Date
--	 <p>Follow up action to Item 1 on 18/04/2019, fill material was covered properly at UV Zone.</p>	--	190426_001	No	--
--	 <p>Follow up action to Item 2 on 18/04/2019, stagnant water was cleared.</p>	--	190426_002	No	--

1	 <p>Stagnant water was accumulated on the drip tray at P1 Zone.</p>	To clear the stagnant water properly	190426_003	Yes	03/05/2019
---	--	--------------------------------------	------------	-----	------------

Appendix I

Landscape and Visual Impact Assessment Checklist

Landscape and Visual Impact Assessment Checklist for Site Audit

Inspection Date: 4 April 2019 Weather: Sunny/ Fine/ Cloudy/ Rainy
Time: 15:00 p.m. Wind: Strong/ Breeze/ Light/ Calm

Item	Description	YES	NO	N/A	Actions/ Remarks
1	Construction Phase				
1.1	Is the detailed tree survey completed prior to construction work?	✓			
1.2	Are trees to be transplanted removed to their final positions?		✓		
1.3	Are the transplants and existing trees to be retained properly protected from damage by stout hoarding positioned as directed by a qualified Landscape Architect?	✓			Eastern side trees: Protective fence has been provided at lot. A few nos. of trees are protected near the site entrance
1.4	Is regular inspection of the retained and transplanted trees made to ensure the effectiveness of the hoarding?	✓			
1.5	Are the TPZ clearly demarcated on site and surrounded by strong fences sturdy enough to withstand impacts from the construction activities?	✓			Except trees far beyond the extent of construction activities, protective fence is noted.
1.6	Are warning signs and notices installed at the fences denoting the “tree protection zone” to prohibit the entry of equipment or construction activities?	✓			
1.7	Are tree labels with clear indication of tree no. and status (e.g. “R”, “T” or “F”) provided for all the trees on site?	✓			
1.8	If protective fencings are not practicable, are the tree root systems adequately protected from soil compaction due to passage of vehicles, equipment or machinery?	✓			
1.9	Are vehicular/foot paths and storage areas designated away from TPZ?	✓			
1.10	Are the trees properly irrigated and sprayed with water to remove the accumulated construction dust during dry season in order to lessen the chances of decline and to			✓	

	maintain the vigour of trees?				
1.11	Are the trees free from any sign of distress, such as dieback, leaf loss, or general decline in tree health or appearance or tree damage with symptoms of construction injury?			✓	Trees in eastern boundary: 1) Dead branches to remove 2) Tear bark/ stubs to be properly pruned.
1.12	Are the trees free from wire or nail and prohibited to be used as anchor for any site activities?	✓			
1.13	Are cutting, trenching, excavating or raising of soil level within the TPZ prohibited?	✓			
1.14	Is improper pruning of the tree branches/roots prohibited?	✓			
1.15	Are the trees free from any tree root damage?	✓			
1.16	Are construction works or operation of machines within the TPZ prohibited?	✓			
1.17	Is the TPZ free from pollution from effluent water, machine petroleum or chemical spillage?	✓			
1.18	Is the excavated topsoil stored and protected on site for reuse for restoration of screen planting works?			✓	The site has previously been reclaimed from ponds. Most of the excavated topsoil is not desirable for reuse due to its inferior quality. Contractor's submitted referencing documents are attached in the checklist dated 4 May, 2018 for information.
1.19	Is the progress of the above activities reported in the monthly EM&A report?	✓			
2	Operational Phase (12 months period from commissioning of the expanded and upgraded works)				
2.1	Is a planting reserve, where locates around the site perimeter of approximately 5m wide, provided to allow a continuous belt of trees to be planted as a visual screen?			✓	
2.2	Is the planting reserve complemented the boundary planting to the existing San Wai			✓	

	STW?				
2.3	Is all new planting maintained for 12 months to ensure proper establishment?			✓	
2.4	Are the trees free from sign of deterioration of tree health and/or structure?			✓	
2.5	Are the trees free from insect pests and disease pathogens?			✓	
2.6	Are the irrigation systems functioning properly and well maintained?			✓	
2.7	Are the tree root systems adequately protected from soil compaction due to storage of materials or operation of machinery?			✓	

Summary/ Remarks:

Follow up actions taken by Contractor for previous comments:

1. Trees at eastern boundary – pruning of dead branches has carried out. Contractor is reminded to carry out proper reduction cut to some of the branches in future to meet the current tree care standard.

The contractor was reminded to rectify the following:

1. Generally, contractor was reminded to keep on the tree protection and maintenance.
2. Stored piles were found under several trees. Contractor was reminded to remove the stored piles and debris underneath.



New Observation:

1. Grade change and construction activities are noted on site. Contractor was reminded not to disturb the TPZ.

Reminders:

1. Contractor was reminded to provide TPZ with robust fence, whenever possible, at the drip line of all retained trees unless the trees are well beyond the extend of construction activities.
2. Contractor was reminded not to disturb trees outside site along the boundary.

Photo Record:

Figure 1	Figure 2
	
<p>General condition of the existing trees at eastern boundary</p>	<p>General condition of the south-west corner of the site. Former trees are removed.</p>



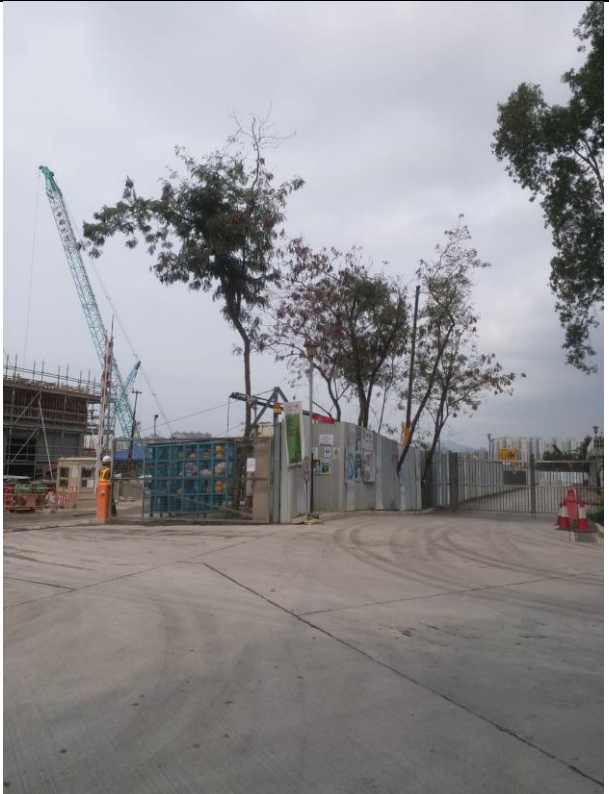


<p>Figure 3</p> 	<p>Figure 4</p> 
<p>Condition of trees at the entrance of the existing treatment plant</p>	<p>All the existing trees near the eastern entrance are removed</p>
<p>Figure 5</p> 	<p>Figure 6</p> 
<p>Existing trees at the site entrance protected by the hoarding fence</p>	<p>One of the spots of stored piles (debris) under the tree</p>

Figure 7	
	
Contractor was reminded not to disturb trees outside site along the boundary	

Signature:

		Signature	Date
Inspected & Recorded by	Registered Landscape Architect		
		Xylem Leung	

Landscape and Visual Impact Assessment Checklist for Site Audit

Inspection Date: 18 April 2019 **Weather:** Sunny/ Fine/ Cloudy/ Rainy
Time: 15:30 p.m. **Wind:** Strong/ Breeze/ Light/ Calm

Item	Description	YES	NO	N/A	Actions/ Remarks
1	Construction Phase				
1.1	Is the detailed tree survey completed prior to construction work?	✓			
1.2	Are trees to be transplanted removed to their final positions?		✓		
1.3	Are the transplants and existing trees to be retained properly protected from damage by stout hoarding positioned as directed by a qualified Landscape Architect?	✓			<p>Eastern side trees: Protective fence has been provided at lot.</p> <p>A few nos. of trees are protected near the site entrance</p>
1.4	Is regular inspection of the retained and transplanted trees made to ensure the effectiveness of the hoarding?	✓			
1.5	Are the TPZ clearly demarcated on site and surrounded by strong fences sturdy enough to withstand impacts from the construction activities?	✓			Except trees far beyond the extent of construction activities, protective fence is noted.
1.6	Are warning signs and notices installed at the fences denoting the “tree protection zone” to prohibit the entry of equipment or construction activities?	✓			
1.7	Are tree labels with clear indication of tree no. and status (e.g. “R”, “T” or “F”) provided for all the trees on site?	✓			
1.8	If protective fencings are not practicable, are the tree root systems adequately protected from soil compaction due to passage of vehicles, equipment or machinery?	✓			
1.9	Are vehicular/foot paths and storage areas designated away from TPZ?	✓			
1.10	Are the trees properly irrigated and sprayed with water to remove the accumulated construction dust during dry season in order to lessen the chances of decline and to			✓	

	maintain the vigour of trees?				
1.11	Are the trees free from any sign of distress, such as dieback, leaf loss, or general decline in tree health or appearance or tree damage with symptoms of construction injury?			✓	Trees in eastern boundary: 1) Dead branches to remove 2) Tear bark/ stubs to be properly pruned.
1.12	Are the trees free from wire or nail and prohibited to be used as anchor for any site activities?	✓			
1.13	Are cutting, trenching, excavating or raising of soil level within the TPZ prohibited?	✓			
1.14	Is improper pruning of the tree branches/roots prohibited?	✓			
1.15	Are the trees free from any tree root damage?	✓			
1.16	Are construction works or operation of machines within the TPZ prohibited?	✓			
1.17	Is the TPZ free from pollution from effluent water, machine petroleum or chemical spillage?	✓			
1.18	Is the excavated topsoil stored and protected on site for reuse for restoration of screen planting works?			✓	The site has previously been reclaimed from ponds. Most of the excavated topsoil is not desirable for reuse due to its inferior quality. Contractor's submitted referencing documents are attached in the checklist dated 4 May, 2018 for information.
1.19	Is the progress of the above activities reported in the monthly EM&A report?	✓			
2	Operational Phase (12 months period from commissioning of the expanded and upgraded works)				
2.1	Is a planting reserve, where locates around the site perimeter of approximately 5m wide, provided to allow a continuous belt of trees to be planted as a visual screen?			✓	
2.2	Is the planting reserve complemented the boundary planting to the existing San Wai			✓	

	STW?				
2.3	Is all new planting maintained for 12 months to ensure proper establishment?			✓	
2.4	Are the trees free from sign of deterioration of tree health and/or structure?			✓	
2.5	Are the trees free from insect pests and disease pathogens?			✓	
2.6	Are the irrigation systems functioning properly and well maintained?			✓	
2.7	Are the tree root systems adequately protected from soil compaction due to storage of materials or operation of machinery?			✓	

Summary/ Remarks:

Follow up actions taken by Contractor for previous comments:

1. Trees at eastern boundary – pruning of dead branches has carried out. Contractor is reminded to carry out proper reduction cut to some of the branches in future to meet the current tree care standard.

The contractor was reminded to rectify the following:

1. Generally, contractor was reminded to keep on the tree protection and maintenance.

New Observation:

1. Grade change and construction activities are noted on site. Contractor was reminded not to disturb the TPZ.

Reminders:

1. Contractor was reminded to provide TPZ with robust fence, whenever possible, at the drip line of all retained trees unless the trees are well beyond the extend of construction activities.

Photo Record:





Figure 1	Figure 2
	
General condition of the existing trees at eastern boundary	General condition of the south-west corner of the site. Former trees are removed.

Figure 3	Figure 4
	
Condition of trees at the entrance of the existing treatment plant	All the existing trees near the eastern entrance are removed
Figure 5	
	
Existing trees at the site entrance protected by the hoarding fence	

Signature:

		Signature	Date
Inspected & Recorded by	Registered Landscape Architect		
		Xylem Leung	

Appendix J

Waste Flow Table

DSD Contract: DC/2013/10
Design, Build and Operate
San Wai Sewage Treatment Works Phase 1



ATAL-Degremont-China Harbour Joint Venture

Name of Department: DSD

Year: 2019

Project: Design, Build and Operate San Wai Sewage Treatment Works - Phase 1

Contract No.: DC/2013/10

Waste Flow Table

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Broken Broken Concrete (see Note ³)	Reused in the Contract (see Note)	Reused in other Projects	Disposed as Public Fill (see Note ⁴)	Imported Fill (see Note ⁴)	Metals	Paper/ cardboard packaging	Plastics (see Note ²)	Chemical Waste	Others, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000 kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000 kg)
Jan	0.988	0.000	0.000	0.000	0.988	0.449	0.000	0.000	0.000	0.000	55.820
Feb	0.632	0.000	0.000	0.000	0.632	0.637	0.000	0.300	0.000	0.000	87.830
Mar	0.750	0.000	0.000	0.000	0.750	0.182	0.000	0.000	0.000	0.000	103.440
Apr	0.625	0.000	0.000	0.000	0.625	0.024	0.000	0.200	0.000	0.000	129.800
May											
Jun											
Jul											
Aug											
Sep											
Oct											
Nov											
Dec											
Total	2.995	0.000	0.000	0.000	2.995	2.990	0.000	0.500	0.000	0.000	376.890

- Notes: (1) The waste flow table shall also include C&D materials that are specified in the Contract to be imported for use at the Site.
(2) Plastics refer to plastic bottles/ containers, plastic sheets/ foam from packaging materials.
(3) Broken concrete for recycling into aggregates.
(4) Assumption: The densities of subbase, Type A, Type B, Rockfill, Soil, Mix Rock and Soil, Reclaimed Asphalt Pave, Slurry are 2.0 ton/m³; the densities of Building debris and special fill materials are 2.1 ton/m³; the densities of Broken Concrete is 2.4 ton/m³.

Appendix K

Environmental Licenses and Permits

Item No.	Nature of Permit / License / Notification	Permit / License/ Notification No.	Date of Issue / Effective of Permit / License	Date of Expiry of Permit / License	Remark (Validity for reporting period only)
1	Environmental Permit	EP-464/2013	18/10/2013	NA	Valid
2	Billing Account for Disposal of Construction Waste	7025330	07/07/2016	NA	Valid
3	Form NA notification (for APCO)	405489	26/07/2016	25/09/2020	Valid
4	Chemical Waste Producer Registration (for Site)	5218-511-A2823-01	23/01/2017	NA	Valid
5	Wastewater Discharge Licence (for WPCO)	WT00026754-2017	28/04/2017	31/01/2022	Valid
6	Construction Noise Permit (for Site)	GW-RN0698-19	13/12/2018	12/06/2019	Valid

Appendix L

Implementation Schedule for Environmental Mitigation Measures (EMIS)

Environmental Mitigation Measures	Location	Implementation Status			
		Implemented	Partially implemented	Not implemented	Not Applicable
Air Quality					
<ul style="list-style-type: none">The working area for the uprooting of trees, shrubs, or vegetation or for the removal of boulders, poles, pillars or temporary or permanent structures should be sprayed with water or a dust suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;	Site Area	√			
<ul style="list-style-type: none">All demolished items (including trees, shrubs, vegetation, boulders, poles, pillars, structures, debris, rubbish and other items arising from site clearance) that may dislodge dust particles should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides within a day of demolition;	Site Area	√			
<ul style="list-style-type: none">Vehicle washing facilities including a high pressure water jet should be provided at every discernible or designated vehicle exit point;	Site Entrance	√			
<ul style="list-style-type: none">The area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;	Site Exit	√			
<ul style="list-style-type: none">Where a site boundary adjoins a road, street, service and or other area accessible to the public, hoarding of not less than 2.4m from ground level should be provided along the entire length of that portion of the site boundary except for a site entrance or exit;	Site Area	√			
<ul style="list-style-type: none">Every main haul road (i.e. any course inside a construction site having a vehicle passing rate of higher than 4 in any 30 minutes) should be paved with concrete, bituminous materials, hardcores or metal plates, and kept clear of dusty materials; or sprayed with water or a dust suppression chemical so as to maintain the entire road surface wet;	Main Haul Road	√			
<ul style="list-style-type: none">The portion of any road leading only to a construction site that is within 30m of a discernible or designated vehicle entrance or exit should be kept clear of dusty materials;	Site Entrance and Exit	√			
<ul style="list-style-type: none">Immediately before leaving a construction site, every vehicle should be washed to remove any dusty materials from its body and wheels;	Site Exit	√			
<ul style="list-style-type: none">Where a vehicle leaving a construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle;	--	√			
<ul style="list-style-type: none">The working area of any excavation or earth moving operation should be sprayed with water or a dusty suppression chemical immediately before, during and immediately after the operation so as to maintain the entire surface wet;	Site Area	√			
<ul style="list-style-type: none">Exposed earth shall be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable	Site Area	√			

surface stabilizer within 6 months after the last construction activity on the construction site or part of the construction site where the exposed earth lies;					
<ul style="list-style-type: none"> Any stockpile of dusty material should be either covered entirely by impervious sheeting; placed in an area sheltered on the top and the 3 sides; or sprayed with water or a dust suppression chemical so as to maintain the entire surface wet. 	Site Area	√			
Noise					
<ul style="list-style-type: none"> Quiet plants should be used in order to reduce the noise impacts to protect the nearby NSRs. 	Site Area	√			
<ul style="list-style-type: none"> Temporary and Movable Noise Barriers should be used in order to reduce the noise impact to the surrounding sensitive receivers 	Site Area	√			
<ul style="list-style-type: none"> Intermittent noisy activities should be scheduled to minimize exposure of nearby NSRs to high levels of construction noise. 	Site Area	√			
<ul style="list-style-type: none"> Idle equipment should be turned off or throttled down. 	Site Area	√			
<ul style="list-style-type: none"> Construction activities should be planned so that parallel operation of several sets of equipment close to a given receiver is avoided 	Site Area	√			
<ul style="list-style-type: none"> Construction plant should be properly maintained and operated. 	Site Area	√			
Water Quality					
<ul style="list-style-type: none"> Exposed stockpiles should be covered with tarpaulin or impervious sheets before a rainstorm occurs; 	Site Area	√			
<ul style="list-style-type: none"> The exposed soil surfaces should also be properly protected to minimize dust emission; 	Site Area	√			
<ul style="list-style-type: none"> The stockpiles of materials should be placed in the locations away from the drainage channel so as to avoid releasing materials into the channel; 	Site Area	√			
<ul style="list-style-type: none"> Wheel washing facilities should be provided at site exits to ensure that earth, mud and debris would not be carried out of the works areas by vehicles; 	Site Exit	√			
<ul style="list-style-type: none"> Provision of site drainage systems and treatment facilities would be required to minimize the water pollution; 	Site Area	√			
<ul style="list-style-type: none"> A discharge license needs to be applied from EPD for discharging effluent from the construction site; 	--	√			
<ul style="list-style-type: none"> The treated effluent quality is required to meet the requirements specified in the discharge license; 	--	√			
<ul style="list-style-type: none"> Provision of chemical toilets is required to collect sewage from workforce. The chemical toilets should be cleaned on a regular basis; 	Chemical Toilet	√			

• A licensed waste collector should be employed to clean the chemical toilets and temporary storage tank on a regular basis;	--	√			
• Illegal disposal of chemicals should be strictly prohibited;	Site Area	√			
• Registration as a chemical waste producer is required if chemical wastes are generated and need to be disposed of. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes;	Site Area	√			
• Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance should be used as a guideline for handling chemical wastes;	Site Area		√		
• The impact from accidental spillage of chemicals can be effectively controlled through good management practices.	Site Area	√			
Waste Management					
• Segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;	Site Area	√			
• To encourage collection of aluminium cans by individual collectors, separate bins should be provided to segregate this waste from other general refuse generated by the workforce;	Site Area	√			
• Any unused chemicals or those with remaining functional capacity should be recycled;	Site Area	√			
• Prior to disposal of C&D waste, it is recommended that wood, steel and other metals be separated for re-use and/or recycling and inert waste as fill material to minimize the quantity of waste to be disposed of to landfill;	Site Area		√		
• Proper storage and site practices to minimize the potential for damage or contamination of construction materials; and	Site Area		√		
• Plan and stock construction materials carefully to minimize amount of waste generated and avoid unnecessary generation of waste.	Site Area	√			
Landscape and Visual					
• Detailed tree survey should have been completed	Site Area	√			
• Trees should be transplanted to their final positions clear of the construction site	--			√	
• Erect site hoarding to protect adjacent vegetation from damage	Site Area	√			

<ul style="list-style-type: none"> Regular inspections of the transplanted trees should be made to ensure the effectiveness of the hoarding 	Site Area	√			
<ul style="list-style-type: none"> Any topsoil excavated during the course of the works should be stored and protected on site for reuse for the restoration and screen planting works 	Site Area			√	

Appendix M

Environmental Site Inspection Schedule

Contract No. DC/2013/10 -
Design, Build and Operate San Wai Sewage Treatment Works – Stage 1
Schedule for Environmental Monitoring and Site Inspection
April 2019


Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2 24hr-TSP 1hr-TSP x 3 NM WQM	3	4 WQM SI	5	6 WQM
7	8 24hr-TSP 1hr-TSP x 3 NM	9 Effluent Sampling WQM	10	11 WQM	12 SI	13 24hr-TSP 1hr-TSP x 3 NM WQM
14	15	16 WQM	17	18 24hr-TSP 1hr-TSP x 3 NM SI WQM	19	20 WQM
21	22	23 Effluent Sampling WQM	24 24hr-TSP 1hr-TSP x 3 NM	25 WQM	26 SI	27 WQM
28	29	30 24hr-TSP 1hr-TSP x 3 NM WQM				

**Contract No. DC/2013/10 -
Design, Build and Operate San Wai Sewage Treatment Works – Stage 1
Schedule for Environmental Monitoring and Site Inspection
May 2019**

Sun	Mon	Tue	Wed	Thu	Fri	Sat
			1	2	3	4
				WQM	SI	WQM
5	6 24hr-TSP 1hr-TSP x 3 NM	7 Effluent Sampling WQM	8	9 WQM	10 SI	11 24hr-TSP 1hr-TSP x 3 NM WQM
12	13	14 WQM	15	16 WQM	17 24hr-TSP 1hr-TSP x 3 NM SI	18 WQM
19	20	21 Effluent Sampling WQM	22	23 24hr-TSP 1hr-TSP x 3 NM WQM	24 SI	25 WQM
26	27	28 WQM	29 24hr-TSP 1hr-TSP x 3 NM	30 WQM	31 SI	

Appendix N

Laboratory Report for Discharge Water



東業德勤測試顧問有限公司 ETS-TESTCONSULT LTD.™

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: etl@ets-testconsult.com
W: www.ets-testconsult.com



TEST REPORT

Testing of Water and Wastewater

Report No. : ENA92790
Date of Issue : 18 April 2019
Page No. : 1 of 1

Information Provided by Customer

Customer Name : ATAL-Degremont-China Harbour Joint Venture
Customer Address : 19/F, China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of Sampling : 09 April 2019
Sample Description : Sample was stored in 1L plastic bottle (for pH and Total Suspended Solids).
Sample was stored in 500ml plastic bottle (for Chemical Oxygen Demand).
Sample for Chemical Oxygen Demand was preserved by adding conc. H_2SO_4 to pH <2.
Sample was collected by the customer and refrigerated after received.

Laboratory Information


Date of Received : 09 April 2019
Date of Testing Period : 09 to 12 April 2019
Lab Ref. No. : W43688

Result

Sample ID	Sample No.	Test	Method Used	Result	Unit
P1a	01	pH	In house method TPE/003/W	8.5	(at 25°C)
		Total Suspended Solids	In house method TPE/006/W	<5*	mg/L
	02	Chemical Oxygen Demand	In house method TPE/002/W	<10	mgO ₂ /L

Remark(s):

- The results relate only to the tested sample as received.
- *200ml sample was used for Total Suspended Solids analysis. PQL of Total Suspended Solids reported less than 5 mg/L.


Approved Signatory : 

LAU, Chi Leung

TPE/001/W

HKAS has accredited this laboratory (Reg. No. HOKLAS 022) under HOKLAS for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. This report shall not be reproduced unless with prior written approval from this laboratory.

- END OF REPORT -



東業德勤測試顧問有限公司 ETS-TESTCONSULT LTD.™

8/F Block B,
Veristrong Industrial Centre,
34-36 Au Pui Wan Street,
Fo Tan, Hong Kong

T: +852 2695 8318
F: +852 2695 3944
E: eti@ets-testconsult.com
W: www.ets-testconsult.com



TEST REPORT

Testing of Water and Wastewater

Report No. : ENA93455
Date of Issue : 02 May 2019
Page No. : 1 of 1

Information Provided by Customer

Customer Name : ATAL-Degremont-China Harbour Joint Venture
Customer Address : 19/F, China Harbour Building, 370-374 King's Road, North Point, Hong Kong
Sample Source : Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works - Stage 1
Sample Type : Wastewater
Date of Sampling : 23 April 2019
Sample Description : Sample was stored in 1L plastic bottle (for pH and Total Suspended Solids).
Sample was stored in 500ml plastic bottle (for Chemical Oxygen Demand).
Sample for Chemical Oxygen Demand was preserved by adding conc. H_2SO_4 to pH <2.
Sample was collected by the customer and refrigerated after received.

Laboratory Information

Date of Received : 23 April 2019
Date of Testing Period : 23 April 2019
Lab Ref. No. : W43781

Result

Sample ID	Sample No.	Test	Method Used	Result	Unit
P1a	01	pH	In house method TPE/003/W	8.2	(at 25°C)
		Total Suspended Solids	In house method TPE/006/W	<5*	mg/L
	02	Chemical Oxygen Demand	In house method TPE/002/W	<10	mgO ₂ /L

Remark(s):

- The results relate only to the tested sample as received.
- *200ml sample was used for Total Suspended Solids analysis. PQL of Total Suspended Solids reported less than 5 mg/L.

Approved Signatory :

LAU, Chi Leung


TPE/001/W

HKAS has accredited this laboratory (Reg. No. HOKLAS 022) under HOKLAS for specific laboratory activities as listed in the HOKLAS directory of accredited laboratories. This report shall not be reproduced unless with prior written approval from this laboratory.

- END OF REPORT -

Figure 1

Locations of Air Quality and Noise Monitoring Stations

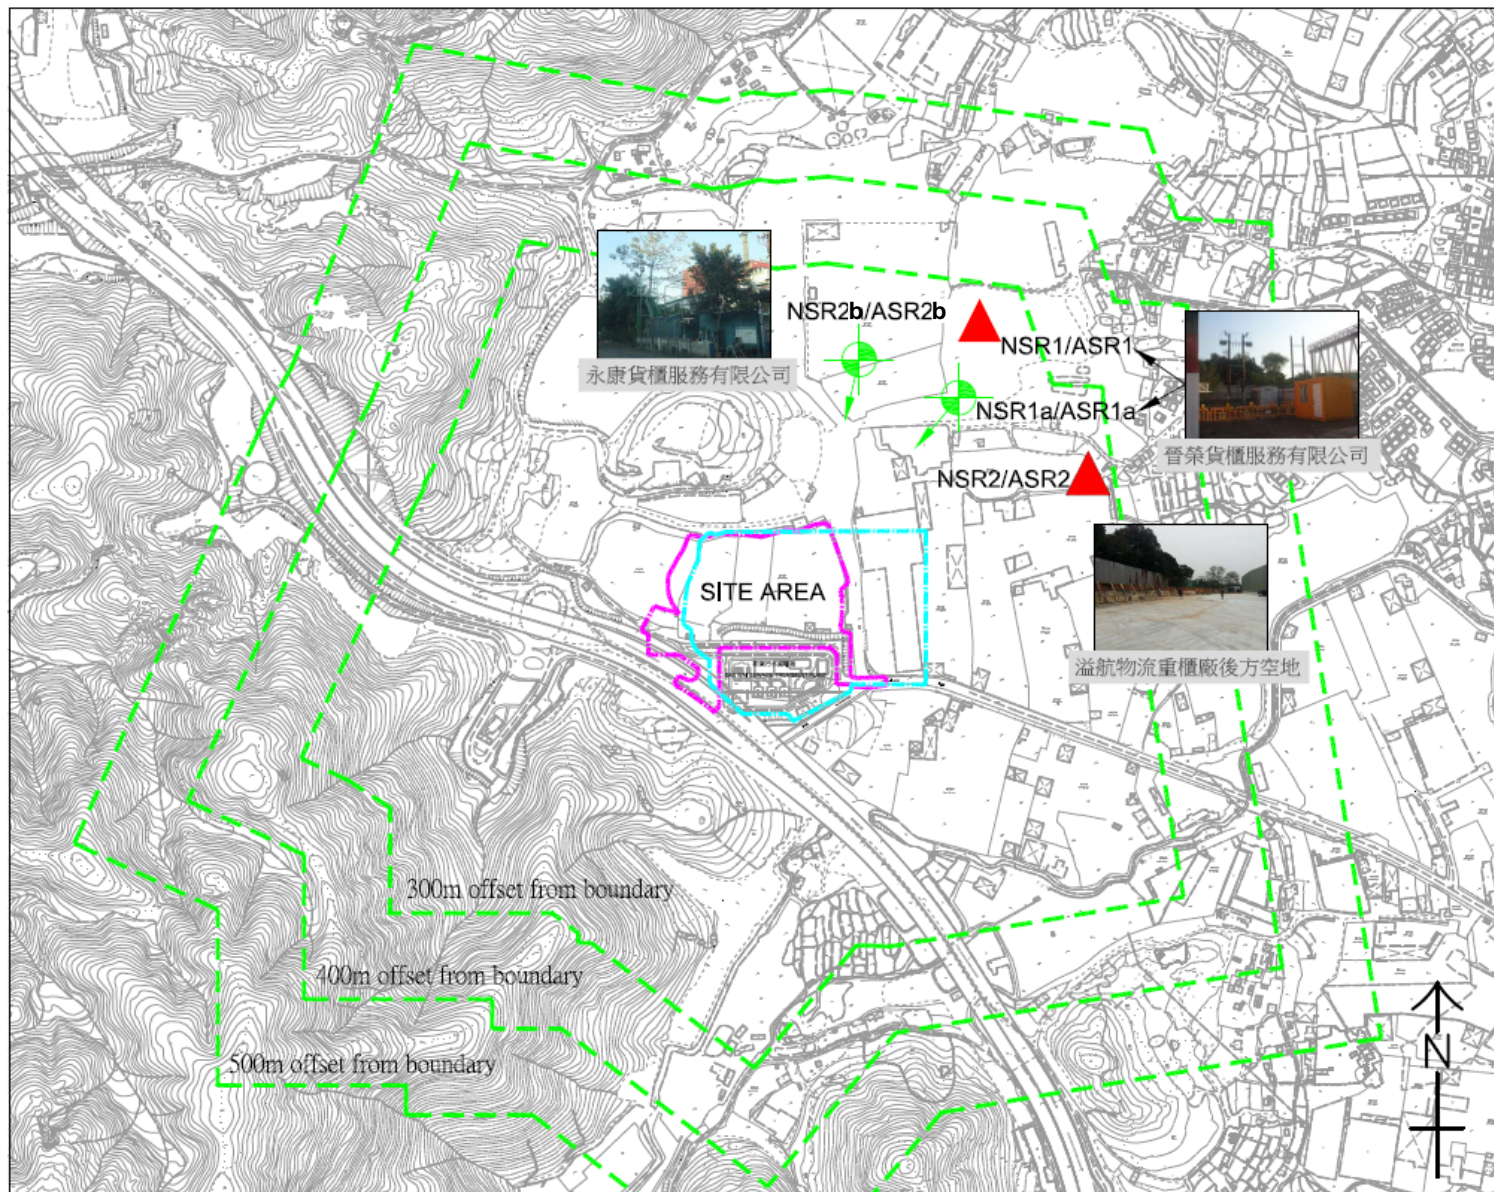


Project: Contract No. DC/2013/10 -Design, Build and Operate San Wai Sewage Treatment Works – Phase 1

Figure 1 Locations of Air Quality and Noise Monitoring Stations

Figure 2


Locations of Water Quality Monitoring Station

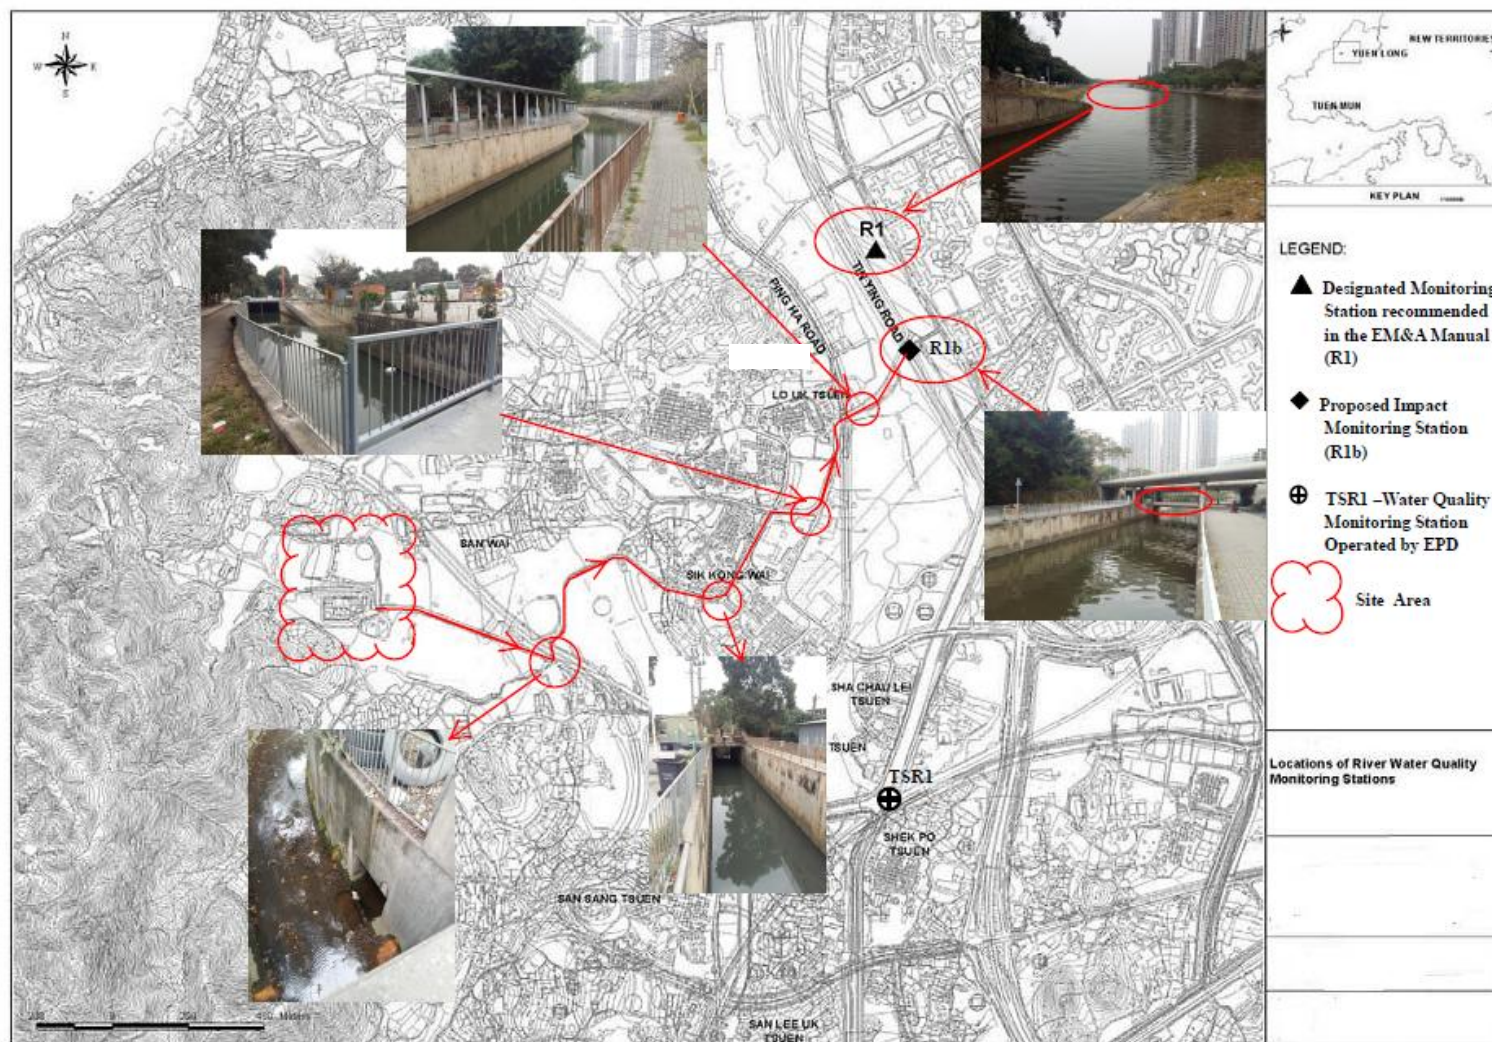

Project: Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Figure 2 Locations of Water Quality Monitoring Station

Figure 3

Location Plan for the Wetsep Treatment Tank



Legend:



Wetsep treatment tank P1a



Wetsep treatment tank P1b

Wetsep treatment tank P8

Project: Contract No. DC/2013/10 - Design, Build and Operate San Wai Sewage Treatment Works – Phase 1
Figure 3 Location Plan for the Wetsep Treatment Tank
