

東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong

Tel : 2695 8318

E-mail : etl@ets-testconsult.com

Fax : 2695 3944

Web site : www.ets-testconsult.com

TEST REPORT

LEADER – WAI KEE (C&T) JOINT VENTURE

**REMAINING ENGINEERING
INFRASTRUCTURE WORKS FOR
PAK SHEK KOK DEVELOPMENT
PACKAGE 2A**

(CONTRACT NO.: TP 37/03)

MONTHLY EM&A REPORT

(MARCH 2008)

Prepared by:

LAW, Sau Yee
Senior Environmental Officer

Approved by:

LAU, Chi Leung
Environmental Team Leader



TABLE OF CONTENTS

Page

EXECUTIVE SUMMARY

1.0	INTRODUCTION	
2.0	PROJECT INFORMATION	
	2.1 Background	1
	2.2 Site Description	1
	2.3 Construction Programme	1
	2.4 Project Organization and Management Structure	1
	2.5 Contact Details of Key Personnel	1 – 2
3.0	CONSTRUCTION PROGRESS IN THIS REPORTING MONTH	2
4.0	AIR QUALITY MONITORING	
	4.1 Monitoring Requirement	3
	4.2 Monitoring Equipment	3
	4.3 Monitoring Parameters, Frequency and duration	3
	4.4 Monitoring Locations and Period	3 – 5
	4.5 Monitoring Methodology	5 – 6
	4.6 Action and Limit levels	6
	4.7 Event-Action Plans	6
	4.8 Results	6
5.0	NOISE MONITORING	
	5.1 Monitoring Requirement	7
	5.2 Monitoring Equipment	7
	5.3 Monitoring Parameters, Frequency and duration	7
	5.4 Monitoring Locations and Period	7 – 8
	5.5 Monitoring Methodology	8 – 9
	5.6 Action and Limit levels	9
	5.7 Event-Action Plans	9
	5.8 Results	9
6.0	WASTEWATER MONITORING	9
7.0	ENVIRONMENTAL NON-CONFORMANCE	
	7.1 Summary of air quality, noise and wastewater monitoring	9 – 10
	7.2 Summary of environmental complaints	10
	7.3 Summary of notification of summons and prosecutions	10
8.0	SITE INSPECTION	
	8.1 Summary of site inspection findings and Action(s) taken by LWKJV and ET	10
	8.2 Status of Environmental Licensing and Permitting	10 – 11
	8.3 Recommendation on Site Inspection findings	11
9.0	WASTE MANAGEMENT	
	9.1 Waste Management Audit	11
	9.2 Records of waste quantities	11
10.0	Implementation Status	
	10.1 Implementation Status of Environmental Mitigation Measures	12
	10.2 Implementation Status of Event and Action Plan	12
	10.3 Implementation Status of Environmental Complaint Handling	12
11.0	CONCLUSION	12
12.0	FUTURE KEY ISSUE	
	12.1 Upcoming EM&A Schedule in coming two months	12 – 13
	12.2 Upcoming Construction Works scheduled in coming two months	13



APPENDIX

- A Organization Chart and Lines of Communication
- B1 Calibration Certificates for Impact Air Quality Monitoring Equipment
- B2 Impact Air Quality Monitoring Results
- B3 Graphical Plots of Impact Air Quality Monitoring Data
- C1 Calibration Certificates for Impact Noise Monitoring Equipment
- C2 Impact Noise Monitoring Results
- C3 Graphical Plots of Impact Noise Monitoring Data
- D Weather Condition
- E Event-Action Plans
- F Construction Programme
- G Construction Site Area
- H Implementation Status of Mitigation Measures and Follow-up Actions during weekly site inspections
- I IEC and RE Comments on Monthly EM&A Report – February 2008

Figure

- Figure 1 Location of Noise Monitoring Locations
- Figure 2 Location of Air Monitoring Locations
- Figure 3 Location of Air and Noise Monitoring Stations at HKIB Staff Accommodation
- Figure 4 Location of Noise Monitoring Station at CUHK Residence No. 10
- Figure 5 Location of Air and Noise Monitoring Stations at Cheung Shue Tan Village

Tables

- 2.1 Contact Details of Key Personnel
- 3.1 Major Construction Activities in this reporting month
- 3.2 Implementation of Environmental Mitigation Measures
- 4.1 Air Quality Monitoring Equipment
- 4.2 Monitoring parameters, duration and frequency of air quality monitoring
- 4.3 Air Quality Monitoring Locations
- 4.4 Monitoring Schedule for air quality monitoring stations
- 4.5 Action and Limit levels for 24-hr TSP and 1-hr TSP
- 5.1 Noise Monitoring Equipment
- 5.2 Duration, Frequency and Parameters of noise monitoring
- 5.3 Noise Monitoring Locations
- 5.4 Monitoring Schedule for noise monitoring stations
- 5.5 Action and Limit levels for noise monitoring
- 7.1 A Cumulative Log of Notification of Summons and Prosecution
- 8.1 The summary of the IEC and ET site inspection findings and Action(s) taken by LWKJV and ET
- 8.2 Summary of environmental licensing and permit status
- 9.1 Summary of Quantities of waste for disposal
- 12.1 Upcoming EM&A Schedule in coming two months
- 12.2 Upcoming Construction Works Scheduled in coming two month



EXECUTIVE SUMMARY

This monthly EM&A report (No.35) has been prepared to document the impact monitoring works conducted for the Contract of the Remaining Engineering Infrastructure Works for Pak Shek Kok Development Package 2A (Contract No: TP 37/03) during the reporting period from 01 to 31 March 2008.

Construction Progress

The major construction works in this reporting month were as below:

<i>Item</i>	<i>Construction Works</i>
1	Remedial / Outstanding works and landscape softworks under Section 1
2	Roadwork at void abutment and existing MLS Bridge
3	Top soil mixing under Section 3
4	Remedial works for loading & unloading area and Ma Liu Shui Subway
5	CCTV inspection for Section 2 and Section 3
6	Outstanding works and defect rectification works for Toilet No.2
7	Landscape softworks at Section 13
8	Construction of crossing at Section 5
9	Drainage pipe rectification works for Section 6
10	Outstanding works at Section 7, 8, 9, and 10

Environmental Monitoring Progress

The summary of the monitoring activities in this monitoring month is listed below:

- Noise Monitoring (Day-time): 4 Occasion at 4 designated locations
- 24-hour TSP Monitoring: 5 Occasions at 3 designated locations
- 1-hour TSP Monitoring: 15 Occasions at 3 designated locations
- Weekly-site inspection: 4 Occasions

Noise Monitoring

No exceedances of Action and Limit levels for noise monitoring were recorded in the reporting month.

Air Monitoring

No exceedances of Action and Limit levels were recorded for 24-hr and 1-hr TSP monitoring in the reporting month.

Wastewater Monitoring

No wastewater monitoring was carried out in this reporting month since the effluent discharge point had been removed.

Site Inspection

Environmental site inspections conducted in this reporting month are presented as follows:

<i>Concerned Parties</i>	<i>Dates of Audit / Inspection in January 2008</i>
<i>Weekly site inspection (ET)</i>	<i>08, 15, 20, 28</i>
<i>Monthly site inspection (IEC/LWKJV/RE)</i>	<i>28</i>



The observations were raised during this reporting month. The site inspection findings are presented as follows:

Item	Aspects	Findings	Action(s) taken by LWKJV	ET Verification
1	Air	Follow up action to the outstanding finding in the previous month, stockpile of sand at Void Abutment was covered during the site inspection on 15/03/08.	No further action should be taken since the finding was improved.	No further ET verification should be taken since the finding was improved.
2	Water	Follow up action to the outstanding finding in the previous month, pesticide was applied to the rain water accumulated inside the drainage channel at Avid Abutment during the site inspection on 08/03/08.	No further action should be taken since the finding was improved.	No further ET verification should be taken since the finding was improved.
3	Chemical	A diesel oil container was noted on the ground at Void Abutment without drip tray during weekly site inspections on 15/03/08 and 20/03/08.	LWKJV replied to provide drip tray for all chemicals.	During the last site inspection on 28/03/08, the container was removed to chemical storage area.

Waste Management

According to weekly site inspection, ET found that the Contractor followed the recommended procedures stipulated in the Waste Management Plan (WMP) on handling and disposal of wastes. 0.25m³ inert C&D materials and 25690kg general refuse were generated in this reporting month. All inert C&D materials were reused in the Contract and other wastes were handling under the instruction and procedure stated in the WMP in this reporting month.

Environmental Complaints

No environmental complaints were received in this monitoring month.

Notification of summons and successful prosecutions

No notification of summons and prosecutions with respect to environmental issues were registered in this reporting month.

Future Key Issues

Since major construction works were completed in March 2008, no future key issue will be considered in the coming month.

1.0 INTRODUCTION

Leader – Wai Kee (C&T) Joint Venture (LWKJV) appointed Environmental Team (ET) of ETS-Testconsult Limited (ETL) to undertake the Environmental Monitoring and Audit (EM&A) for Remaining Engineering Infrastructure Works for Pak Shek Kok Development Package 2A (Contract No.: TP 37/03).

In accordance with the Section 10 of Environmental Permit to Construct and Operate a Designate Project (EP-108/2001/AEP-108/2001), EM&A programme as set out in the EM&A Manual is required to be implemented. In accordance with the EM&A manual, environmental monitoring of air quality and noise is required for the Project. The EM&A requirement for each parameter are described in details in subsequent sections, including:

- All monitoring parameters;
- Action and Limit levels for all environmental parameters;
- Event-Action Plans;
- Environmental mitigation measures, as recommended in the project EIA study report;
- Environmental requirements in contract documents.

This monthly EM&A report summarizes the impact monitoring results and audit findings of the EM&A program during the reporting period from 01 to 31 March 2008.

2.0 PROJECT INFORMATION

2.1 Background

Remaining Engineering Infrastructure Works for Pak Shek Kok Development Package 2A (Contract No.: TP 37/03) was planned and designed by the Civil Engineering and Development Department (CEDD).

As the main Contractor of the captioned project: contracted by, LWKJV will follow the environmental monitoring recommendation stated at the EM&A Manual that was prepared with reference to the EIA Study for Feasibility Study on the Pak Shek Kok Development Area (PSKDA) Environmental Monitoring and Audit Manual under Agreement No. CE 90/96.

2.2 Site Description

Generally, the construction site is located at Pak Shek Kok development area. Surrounding the construction site, there are two air sensitive receivers: HKIB Staff Accommodation and Cheung Shue Tan Village and three noise sensitive receivers: HKIB Staff Accommodation, CUHK Residence No.10 and Cheung Shue Tan Village.

Figure 1 and 2 show the noise and air monitoring locations of this project.

2.3 Construction Programme

Details of construction programme are shown in Appendix F.

2.4 Project Organization and Management Structure

The organization chart and lines of communication with respect to the on-site environmental management and monitoring program are shown in Appendix A.

2.5 Contact Details of Key Personnel

The key personnel contact names and telephone numbers, and construction programme are shown in table 2.1.

Table 2.1 Contact Details of Key Personnel

Organization	Project Role	Name of Key Staff	Tel. No.	Fax No.
CEDD	Mr. M. S. Lam	Employer	2158 5630	2693 2918
Hyder	Mr. Herman Fong	Engineer	2603 6638	2603 7883
LWJV	Mr. Joe Yip	Site Representative	2442 1123	2442 9733
Hyder	Mr. Alexi Bhanja	Independent Environmental Checker	2911 2233	2805 5028
ETL	Mr. C.L. Lau	Environmental Team Leader	2946 7791	2695 3944

3.0 CONSTRUCTION PROGRESS IN THIS REPORTING MONTH

The site area of this project is shown in Appendix G.

A summary of the major construction activities undertaken in this monitoring month is shown in Table 3.1. The implementation of corresponding mitigation measures is summarized in Table 3.2.

Table 3.1 Major Construction Activities in this reporting month

Item	Construction Activities
1	Remedial / Outstanding works and landscape softworks under Section 1
2	Roadwork at void abutment and existing MLS Bridge
3	Top soil mixing under Section 3
4	Remedial works for loading & unloading area and Ma Liu Shui Subway
5	CCTV inspection for Section 2 and Section 3
6	Outstanding works and defect rectification works for Toilet No.2
7	Landscape softworks at Section 13
8	Construction of crossing at Section 5
9	Drainage pipe rectification works for Section 6
10	Outstanding works at Section 7, 8, 9, and 10

Table 3.2 Implementation of Environmental Mitigation Measures

General construction works	<ul style="list-style-type: none"> • Effective water sprays used on the site at potential dust emission sources such as haul roads and unpaved areas; • The heights from which fill materials are dropped should be controlled to a practical height to minimize the fugitive dust arising from unloading; • Minimize of exposed soil areas to reduce the potential for increased siltation and contamination of run-off; • Water, hydro-seed or cover the open stockpile and exposed loose soil areas by using clean tarpaulin sheets; • Provide proper and efficient drainage facilities (e.g. wheel washing facilities) and sedimentation system to ensure that site runoff should be treated before discharged to drains; • Remove the sand/rubbish accumulated in the drain/channel regularly; • Provide good site practice (e.g. selection of quieter plant and working methods and reduction in number of plant operating in critical areas close to NSRs) to limit noise emissions at source; • Remove the construction waste accumulated inside or outside the site regularly.
----------------------------	---

4.0 AIR QUALITY MONITORING

4.1 Monitoring Requirement

1-hour and 24-hour TSP monitoring were required to be conducted to monitor the air quality, at designated monitoring locations:

- HKIB Staff Accommodation (on ground floor near the entrance facing south-east);
- Cheung Shue Tan Village (near the outer building, temple) for 1-hr TSP monitoring;
- Cheung Shue Tan Village (in front of Man Kee Store) for 24-hr TSP monitoring;
- Near Wen Chih Tang at the CUHK.

4.2 Monitoring Equipment

Continuous 24-hour TSP air quality monitoring was performed using a GMWS2310 High Volume Air Sampler (HVS) located at each of the designated monitoring station. One portable dust meter was used to carry out the 1-hour TSP monitoring. Table 4.1 summarizes the equipment used in the air quality monitoring programme. A copy of the calibration certificates for the HVS and portable dust meter are attached in Appendix B1.

Table 4.1 Air Quality Monitoring Equipment

Equipment	Model and Make
HVS	Greasby GMWS2310
Calibrator	Tisch TE-5025A
1-hour TSP Dust Meter	TSI Model 8520 Dust Trak™ Aerosol Monitor

4.3 Monitoring Parameters, Frequency and Duration

Table 4.2 summarizes the monitoring parameters, monitoring duration and frequencies of air quality monitoring.

Table 4.2 Monitoring parameters, duration, frequencies of impact air quality monitoring

Parameter	Duration	Frequency
24-hr TSP	24 hr (0000-2400)	Once every six days
1-hr TSP	1 hr (0700-1900)	Three times every six days

4.4 Monitoring Locations and Schedule

Table 4.3 tabulates the air quality monitoring locations of this project.

Table 4.3 Air quality monitoring locations

Monitoring stations	Locations
AM1	HKIB Staff Accommodation (on ground floor near the entrance facing south-east) for 1-hr TSP monitoring
AM3	Cheung Shue Tan Village (near the outer building, temple) for 1-hr TSP monitoring
AM3A	Cheung Shue Tan (in front of Man Kee Store) for 24-hr TSP monitoring
AM5	Near Wen Chih Tang at the CUHK

The air quality monitoring schedule for 24-hr and 1-hr TSP monitoring at designated monitoring locations is summarized in table 4.4.



Table 4.4 Monitoring Schedule for the air quality monitoring stations

Air quality monitoring stations	Location	Monitoring Period						
		24-hr TSP				1-hr TSP		
		Start		Finish		Date	Start	Finish
		Date	Time	Date	Time			
AM1	HKIB Staff Accommodation					01/03/08	10:00	11:00
						04/03/08	13:02	14:02
						06/03/08	15:00	16:00
						08/03/08	13:00	14:00
						11/03/08	08:30	09:30
						12/03/08	13:00	14:00
						13/03/08	08:30	09:30
						15/03/08	11:00	12:00
						18/03/08	11:00	12:00
						19/03/08	17:00	18:00
						20/03/08	09:15	10:15
						25/03/08	18:00	19:00
						27/03/08	18:00	19:00
						29/03/08	13:00	14:00
				31/03/08	14:25	15:25		
AM3	Cheung Shue Tan Village (Near the outer building, temple)					01/03/08	13:00	14:00
						04/03/08	15:20	16:20
						06/03/08	16:20	17:20
						08/03/08	15:30	16:30
						11/03/08	16:15	17:15
						12/03/08	09:15	10:15
						13/03/08	16:40	17:40
						15/03/08	14:15	15:15
						18/03/08	13:00	14:00
						19/03/08	14:30	15:30
						20/03/08	14:15	15:15
						25/03/08	15:45	16:45
						27/03/08	13:00	14:00
						29/03/08	08:45	09:45
				31/03/08	11:00	12:00		
AM5	Near Wen Chih Tang at the CUHK					01/03/08	14:20	15:20
						04/03/08	14:08	15:08
						06/03/08	17:35	18:35
						08/03/08	14:15	15:15
						11/03/08	17:30	18:30
						12/03/08	10:30	11:30
						13/03/08	17:55	18:55
						15/03/08	13:00	14:00
						18/03/08	15:30	16:30
						19/03/08	15:45	16:45
						20/03/08	13:00	14:00
						25/03/08	16:55	17:55
						27/03/08	16:50	17:50
						29/03/08	14:15	15:15
				31/03/08	13:10	14:10		
AM1	HKIB Staff Accommodation	06/03/08	09:10	07/03/08	08:30			
		12/03/08	10:55	13/03/08	09:54			
		18/03/08	11:07	19/03/08	10:22			
		25/03/08	08:42	26/03/08	08:16			
		31/03/08	14:30	01/04/08	14:05			
AM3A	Cheung Shue Tan (in front of Man Kee Store)	06/03/08	08:40	07/03/08	08:32			
		12/03/08	10:24	13/03/08	10:24			
		18/03/08	13:10	19/03/08	12:22			
		25/03/08	08:15	26/03/08	08:15			
		31/03/08	11:05	01/04/08	11:05			
AM5	Near Wen Chih Tang at the CUHK	06/03/08	09:00	07/03/08	08:28			
		12/03/08	10:38	13/03/08	10:10			
		18/03/08	15:40	19/03/08	15:32			
		25/03/08	08:35	26/03/08	08:39			
		31/03/08	13:15	01/04/08	12:28			

4.5 Monitoring Methodology

24-hour TSP Monitoring

Instrumentation

High volume sampler, as HVS, (Greasby GMWS2310) complete with appropriate sampling inlets are employed for 24-hour TSP. The sampler is composed of a motor, a filter holder, a flow controller and a sampling inlet and its performance specification complies with that required by USEPA standard Title 40, Code of Federation Regulations Chapter 1 (Part 50).

Installation

The installation of HVS refers to the requirement stated in EM&A Manual.

Operation/Analytical Procedures

Operating/analytical procedures for the operation of HVS are as below:

Prior to the commencement of the dust sampling, the flow rate of the high volume sampler was properly set (between 0.6m³/min and 1.7m³/min.) in accordance with the manufacturer's instruction to within the range recommended in USEPA Standard Title 40, CFR Part 50.

- For TSP sampling, fiberglass filters (GA-55) were used.
- The power supply was checked to ensure the sampler worked properly.
- On sampling, the sampler was operated 5 minutes to establish thermal equilibrium before placing any filter media at designated air monitoring station.
- The filter holding frame was then removed by loosening the four nuts and carefully a weighted and conditioned filter was centered with the stamped number upwards, on a supporting screen.
- The filter was aligned on the screen so that the gasket formed an air-tight seal on the outer edges of the filter. Then the filter holder frame was tightened to the filter holder with swing bolts. The applied pressure should be sufficient to avoid air leakage at the edges.
- The programmable timer will be set for a sampling period of 24 hours. Information was recorded on the record sheet, which included the starting time, the weather condition and the filter number (the initial weight of the filter paper can be found out by using the filter number.).
- After sampling, the filter was transferred from the filter holder of the HVS to a sealed plastic bag and sent to the laboratory for weighting. The elapsed time was also recorded.
- Before weighting, all filters were equilibrated in a desiccator for 24 hour with the temperature of 25°C ± 3°C and the relative humidity (RH) <50% ±5%.

Maintenance & Calibration

- The HVS and their accessories should be maintained in good working condition, such as replacing motor brushes routinely and checking electrical wiring to ensure a continuous power supply.
- HVS should be calibrated at bi-monthly intervals.

1-hour TSP Monitoring

Measuring Procedures

The measuring procedures of the 1-hr dust meter are in accordance with the Manufacturer's instruction Manual as follows:

- Set POWER to ON, check the battery indicator to ensure whether the power supply is enough to conduct the TSP monitoring;
- Calibrate the dust meter by zero check;
- Set the TIME CONSTANT of the dust meter;
- Press SAMPLE to start the TSP monitoring;
- Record the maximum, minimum and average reading directly from the dust meter by press STATISTICS when monitoring complete.

Maintenance & Calibration

- 1-hr dust meter should be checked at 3-month intervals and calibrated at 1-year intervals throughout all stages of impact air quality monitoring.

Wind Data Monitoring

Wind data (wind speed and wind direction) were directly extracted from Sha Tin Station (located at Sha Tin Race Course) of Hong Kong Observatory. All wind data during this reporting month are shown in Appendix D.

4.6 Action and Limit Levels

Action and Limit levels for 24-hr TSP and 1-hr TSP derived as illustrated in Table 4.5.

Table 4.5 Action and Limit Levels for 24-hr TSP and 1-hr TSP

Monitoring Location	24-hr TSP ($\mu\text{g}/\text{m}^3$)		1-hr TSP ($\mu\text{g}/\text{m}^3$)	
	Action Level	Limit Level	Action Level	Limit Level
AM1	164 *	260 *	325 *	500 *
AM3	---	---	306 **	500 **
AM3A	183 **	260 **	---	---
AM5	174	260	329	500

* = Reference to the information contained in the Baseline Monitoring Report submitted under the "Advance Engineering Infrastructure Works for Pak Shek Kok Development – Southern Access Road and Sewage Pumping Station No.3.

** = Reference to the information contained in the Baseline Monitoring Report submitted under the "Remaining Engineering Infrastructure Works for Pak Shek Kok Development Package 1 – Contract No. TP 35/02.

4.7 Event-Action Plans

Please refer to Appendix E for details.

4.8 Results

4.8.1 24-hour TSP Monitoring

All monitoring data of 24-hour TSP monitoring is provided in Appendix B2. Graphical presentation of 24-hour TSP monitoring results for the reporting month is shown in Appendix B3.

No exceedances of Action and Limit Level of 24-hour TSP monitoring results were recorded during the reporting month.

4.8.2 1-hour TSP Monitoring

1-hour TSP monitoring was carried out at monitoring stations, AM1 and AM3 in the reporting month. All monitoring data of 1-hour TSP monitoring is provided in Appendix B2. Graphical presentation of 1-hour TSP monitoring results for the reporting month is shown in Appendix B3.

No exceedances of Action and Limit Level of 1-hour TSP monitoring results were recorded during the reporting month.

5.0 Noise Monitoring

5.1 Monitoring Requirements

As the requirement in EM&A Manual, noise monitoring was conducted at designated monitoring locations:

- HKIB Staff Accommodation (on ground floor near the entrance facing south-east);
- Cheung Shue Tan Village (near the outer building, temple);
- CUHK Residence No.10;
- Near Wen Chih Tang at the CUHK.

5.2 Monitoring Equipment

Integrating Sound Level Meters were used for noise monitoring. They were Type 1 sound level meters capable of giving a continuous readout of the noise level reading including equivalent continuous sound pressure level (L_{eq}) and percentile sound pressure level (L_x). They comply with International Electro technical Commission Publications 651:1979 (Type1) and 804:1985 (Type1), and speed in m/s was used to monitor the wind speed.

Table 5.1 summarized noise monitoring equipment model being used. A copy of the calibration certificates for noise meters and calibrator are attached in Appendix C1.

Table 5.1 Noise Monitoring Equipment

Equipment	Model
Integrating Sound Level Meter	Rion NL-31 Sound Level Meter
Calibrator	Rion NL-73 Sound Level Calibrator
Portable Wind Speed Indicator	TSI Model 8340-M Air Velocity Meter

5.3 Monitoring Parameters, duration and Frequency

Noise monitoring for the A-weighted levels L_{eq} , L_{10} and L_{90} were recorded. The following guide on the regular monitoring frequency for each monitoring station on a per week basis when noise generating activities are underway:

- One set of measurements between 0700-1900 hours on normal weekdays (6 consecutive $L_{eq(5-min)}$);
- One set of measurements between 1900-2300 hours (3 consecutive $L_{eq(5-min)}$)*;
- One set of measurements between 2300-0700 hours of next day (3 consecutive $L_{eq(5-min)}$)*;
- One set of measurements between 0700-1900 hours on holidays (3 consecutive $L_{eq(5-min)}$)*.

(*): Noise monitoring to be conducted only when there is construction work.

Duration, frequencies and parameters of noise measurement are presented in Table 5.2.

Table 5.2 Duration, Frequencies and Parameters of Noise Monitoring

Time period	Duration/min	Parameters	Frequency
Day-time: 0700-1900 hrs on normal weekday	30	L_{eq} , L_{10} , L_{90}	Once per week
Evening-time: 1900-2300 hrs	15	L_{eq} , L_{10} , L_{90}	Once per week
Night-time: 2300-0700 hrs of next day	15	L_{eq} , L_{10} , L_{90}	Once per week
Holiday: 0700-1900 hrs	15	L_{eq} , L_{10} , L_{90}	Once per week

5.4 Monitoring Locations and Period

In this reporting month, there were five noise monitoring locations: HKIB Staff Accommodation, Cheung Shue Tan Village, CUHK Residence No.10 and Near Wen Chih Tang at the CUHK. The location of the monitoring stations are described in Table 5.3 and depicted in Figure 1.

Table 5.3 Noise Monitoring Locations

Noise Monitoring station	Location
NM1	HKIB Staff Accommodation (on ground floor near the entrance facing south-east)
NM2	CUHK Residence No.10
NM3	Cheung Shue Tan Village (near the outer building, a temple)
NM8	Near Wen Chih Tang at the CUHK

The noise-monitoring programme of monitoring locations (Day-time, Evening-time, Holiday and Night-time) is summarized in Table 5.4.

Table 5.4 Monitoring Periods for noise monitoring stations

Monitoring stations	Monitoring Period							
	Day-time		Evening-time		Holiday		Night-time	
NM1	04/03/08	13:08	---	---	---	---	---	---
	11/03/08	08:35	---	---	---	---	---	---
	18/03/08	11:02	---	---	---	---	---	---
	25/03/08	18:05	---	---	---	---	---	---
NM2	04/03/08	13:50	---	---	---	---	---	---
	11/03/08	09:15	---	---	---	---	---	---
	18/03/08	14:15	---	---	---	---	---	---
	25/03/08	16:15	---	---	---	---	---	---

Monitoring stations	Monitoring Period							
	Day-time		Evening-time		Holiday		Night-time	
NM3	04/03/08	15:22	---	---	---	---	---	---
	11/03/08	16:20	---	---	---	---	---	---
	18/03/08	13:02	---	---	---	---	---	---
	25/03/08	15:30	---	---	---	---	---	---
NM8	04/03/08	14:30	---	---	---	---	---	---
	11/03/08	17:35	---	---	---	---	---	---
	18/03/08	15:32	---	---	---	---	---	---
	25/03/08	17:10	---	---	---	---	---	---

5.5 Monitoring Procedures and Calibration Details

Operation/Analysis Procedures

- The Sound Level Meter was set on a tripod at a height of 1.2m above the ground.
- For free field measurement, the meter was positioned away from any nearby reflective surfaces.
- The battery condition was checked to ensure the correct functioning of the meter.
- Parameters such as frequency weighting, the time weighting and the measurement time were set as follows:
 - Frequency weighting: A
 - Time weighting: Fast
 - Time measurement : 5 mins
- Prior to and after each noise measurement, the meter was calibrated using a Calibrator for 94 dB at 1000HZ. If the difference in the calibration level before and after measurement was more than 1dB(A), the measurement would be considered invalid and repeat measurement would be required after re-calibration or repair of the equipment.
- The wind speed was frequently checked with a portable wind meter.
- During the monitoring period, the Leq, L10 and L90 were recorded. In addition, site conditions and noise sources were recorded on a standard record sheet.
- Free Field correction to the measurements should be made. Correction factor of +3dB(A) should be made to the free Field measurements.
- Noise monitoring would be cancelled in the presence of fog, rain, wind with a steady speed exceeding 5m/s, or wind gusts exceeding 10m/s.

Maintenance and Calibration

- The microphone head of the sound level meter and calibrator is cleaned with soft cloth at quarterly intervals.
- The meter is sent to be supplier or HOKLAS laboratory to check and calibrated at yearly intervals.

5.6 Action and Limit Levels

The Action and Limit levels for noise levels derived as illustrated in Table 5.5.

Table 5.5 Action and Limit Levels for noise monitoring

Time Period	Time Period	Action	Limit
Normal hours	0700-1900 hrs on normal weekdays	When one documented complaint is received	75 dB(A) *
Holiday	0700-1900 hrs on holidays		70 dB(A) **
Evening-time	1900-2300 hrs on all other days		55 dB(A) **
Night-time	2300-0700 hrs of next day		55 dB(A) **

* = Reduce to 70 dB(A) for schools and 65 dB(A) during school examination periods.

** = Area Sensitivity Rating (ASR) C is selected from the "Technical Memorandum on Noise from Construction Work Other Than Percussive Piling".

5.7 Event-Action Plans

Please refer to the Appendix E for details.

5.8 Results

Only Day-time noise monitoring were carried out at monitoring stations in this reporting month. No Evening-time, Night-time and Holiday noise monitoring were required since no construction works were processed during the night-time period. All noise levels are provided in Appendix C2. Graphical presentation of the monitoring results for the reporting month is shown in Appendix C3.

No Day-time noise monitoring results at all monitoring stations exceeded the Action Level since no documented complaints on noise issue were received in this reporting month. Besides, no exceedances in Limit Level were recorded according to the results from Day-time noise monitoring.

6.0 WASTEWATER MONITORING

Effluent Discharge License of this Project is valid from 06 December 2004 (Discharge Licence No.: 3246-Part A and Part B).

During this reporting month, no wastewater monitoring was required to be carried out since the wastewater monitoring had been carried out on 18 June 2007 and the Discharge Licence required carrying out wastewater monitoring at effluent discharge point quarterly.

No wastewater monitoring was carried out in this reporting month since the effluent discharge point had been removed.

7.0 ENVIRONMENTAL NON-CONFORMANCE

7.1 Summary of environmental monitoring

No exceedances of Action and Limit Level of 24-hour and 1-hour TSP monitoring results were recorded during the reporting month.

No day-time noise level measured at all monitoring stations exceeded the Action and Limit Level in the reporting month. No evening-time, night-time and holiday noise monitoring were required since no construction works were processed during these periods.

No wastewater monitoring was carried out in this reporting month since the effluent discharge point had been removed.

7.2 Summary of Environmental Complaints

No environmental complaints were received in this monitoring month.

7.3 Summary of Notification of Summons and Prosecution

There was no notification of summons respect to environmental issues registered in this month.

8.0 SITE INSPECTION

Weekly site inspections were carried out by the ET in this reporting month (08, 15, 20 and 28 March 2008). Monthly joint site inspection at 28 March 2008 was carried out by Engineer's Representative, IEC and LWKJV. The implementation status of the mitigation measures on site inspections in this reporting month is presented in Appendix H.

8.1 Summary of the site inspection findings and Action(s) taken by LWKJV and ET

Summaries of the site inspection findings in this reporting month are shown in Table 8.1.

Table 8.1 The summary of the site inspection findings and Action(s) taken by LWKJV and ET

Item	Aspects	Findings	Action(s) taken by LWKJV	ET Verification
1	Air	Follow up action to the outstanding finding in the previous month, stockpile of sand at Void Abutment was covered during the site inspection on 15/03/08.	No further action should be taken since the finding was improved.	No further ET verification should be taken since the finding was improved.
2	Water	Follow up action to the outstanding finding in the previous month, pesticide was applied to the rain water accumulated inside the drainage channel at Avid Abutment during the site inspection on 08/03/08.	No further action should be taken since the finding was improved.	No further ET verification should be taken since the finding was improved.
3	Chemical	A diesel oil container was noted on the ground at Void Abutment without drip tray during weekly site inspections on 15/03/08 and 20/03/08.	LWKJV replied to provide drip tray for all chemicals.	During the last site inspection on 28/03/08, the container was removed to chemical storage area.

8.2 Status of Environmental Licensing and Permitting

All permits/licenses valid in this reporting month are summarized in Table 8.2.

Table 8.2 Summary of environmental licensing and permit status

Description	Permit No.	Valid Period		Section
		From	To	
Construction Noise Permit for the Construction Site at Pak Shek Kok Development Package 2A, Tai Po / Ma Liu Shui, N.T.	GW-RN0559-07	06/01/08	29/06/08	<u>Group A</u> Two Poker, vibratory, hand-held (CNP170) Two Concrete lorry mixer (CNP044) One Excavator, tracked (CNP081) <u>Group B</u> One Asphalt Paver (CNP004) One Roller, Vibratory (CNP186) One Road Roller (CNP185) One Dump Truck (CNP067) <u>Group C</u> One Dump Truck (CNP067) One Excavator, tracked (CNP081) One Crane, mobile (diesel) (CNP048) One Lorry with crane
Wastewater Discharge License	3246 – Part A	01/11/06	31/12/09	Discharge of trade Effluent, surface run-off and all other wastewater arising from the construction site and sedimentation tank to Coastal water or communal drain for the carriage of surface drainage water.
Wastewater Discharge License	3246 – Part B	06/12/04	05/12/09	Discharge of trade Effluent, surface run-off and all other wastewater arising from the construction site and on-site aerobic waste water treatment system to soak-away pit.
Chemical Waste Producer	5113-729-LL 1113-01	24/09/04	---	Spent lubricating oil, spent battery parts containing heavy metals

8.3 Recommendations on site inspection findings in Site Inspections of this month

Based on the site inspection findings, the recommendations are as below:

- All stockpiles should be covered with clean tarpaulin sheets, spraying with water or hydro-seeding to avoid wind and water erosion;
- Size of tarpaulin sheet should be larger than surface size of stockpile in order to resume normal function of tarpaulin sheet;
- The heights from which fill materials are dropped should be controlled to a practical height to minimize the fugitive dust arising from unloading or provide a canvas with larger surface area;
- Minimize of exposed soil areas to reduce the potential for increased siltation and contamination of run-off;
- Checking and maintaining all the site machines to prevent dust emission;
- Bigger sumpit for increasing wastewater input should provide for any necessary;

- Providing briefing to the concerned site staff on remedial actions, such as handling method of chemicals and chemical waste;
- Regular maintenance of excavator or any diesel cater machines should be provided in order to avoid any possible smoke nuisance; and
- Provide good site practice (e.g. selection of quieter plant and working methods and reduction in number of plant operating in critical areas close to NSRs) to limit noise emissions at source; Maintain good waste management at the site.

9.0 WASTE MANAGEMENT

9.1 Waste Management Audit

Waste management audit was carried out by the ET on a weekly basis. The implementation status of the mitigation measures on waste management in this reporting month is presented in Appendix H.

9.2 Records of Waste Quantities

The types of wastes arising from the construction work are classified into the following:

- General refuses;
- Chemical waste;
- Construction & demolition (C&D) material.

The quantities of waste for disposal in this month are summarized in Table 9.1.

Table 9.1 Summary of Quantities of Waste for Disposal in this reporting month

Type of Waste		Quantity	Disposal Location	Cumulative Quantity
Inert C&D Materials	Total Quantity Generated (m ³)	0.25	Reused in the Contract	129243.75
	Broken Concrete (m ³)	0.25	N/A	1231.75
	Reused in the Contract (m ³)	0	N/A	128100
	Reused in other Projects (m ³)	0	N/A	0
	Disposal as Public Fill (m ³)	0	N/A	0
C&D Waste	Metals (1000kg)	0	N/A	37.705
	Paper/Cardboard Packaging (1000kg)	0	N/A	2.806
	Plastics (1000kg)	0	N/A	0.083
	Chemical Waste (1000kg)	0	N/A	3.7
	Other, e.g. General Refuse (1000kg)	25.69	SENT	1994.06

10.0 IMPLEMENTATION STATUS

10.1 Implementation Status of Environmental Mitigation Measures

LWKJV has been implementing the required environmental mitigation measures according to the Mitigation Protection Measures stated in Implementation Schedule of the EM&A Manual. The implementation status of the environmental mitigation measures in this reporting month is presented in Appendix H.

Air Quality

The Contractor was reminded to water or cover all the stockpiles by using clean tarpaulin sheets. The Contractor was also reminded to cleanup the access road regularly to avoid dust emission and provide effective wheel washing facilities.

Noise

All mitigation measures stated in Appendix H were implemented properly in this reporting month.

Water Quality

The Contractor was reminded to provide more effort to implement mitigation measures, such as diverting site runoff to suitable treatment processes before discharge, sedimentation system and drainage facilities.

Waste Management

LWKJV has been implementing most mitigation measures on waste management.

10.2 Implementation Status of Event and Action Plan

There were no exceedances in air quality and noise monitoring parameters recorded in this monitoring month. No further mitigation measures were required.

10.3 Implementation Status of Environmental Complaint Handling

No complaints had been received during this monitoring month.

11.0 CONCLUSION

Impact monitoring of air quality and noise were carried out at designated locations in accordance with the EM&A Manual in this reporting month.

According to the summary of air and noise monitoring results, no exceedances of Action and Limit Level of 24-hour and 1-hour TSP monitoring results were recorded during the reporting month. Besides, No Day-time noise level measured at all monitoring stations exceeded the Action and Limit Level in the reporting month. No Evening-time, Night-time and Holiday noise monitoring were required since no construction works were processed during these periods.

No wastewater monitoring was carried out in this reporting month since the effluent discharge point had been removed.


According to the ET weekly site inspection and IEC monthly site audit carried out this month, it indicated that site practices of the LWKJV were generally undertaken in an environmentally acceptable manner and the overall site environmental performance was satisfactory.

Since major construction works were completed in March 2008, no impact monitoring will be required in the coming month.




Appendix A

Organization Chart and Lines of Communication

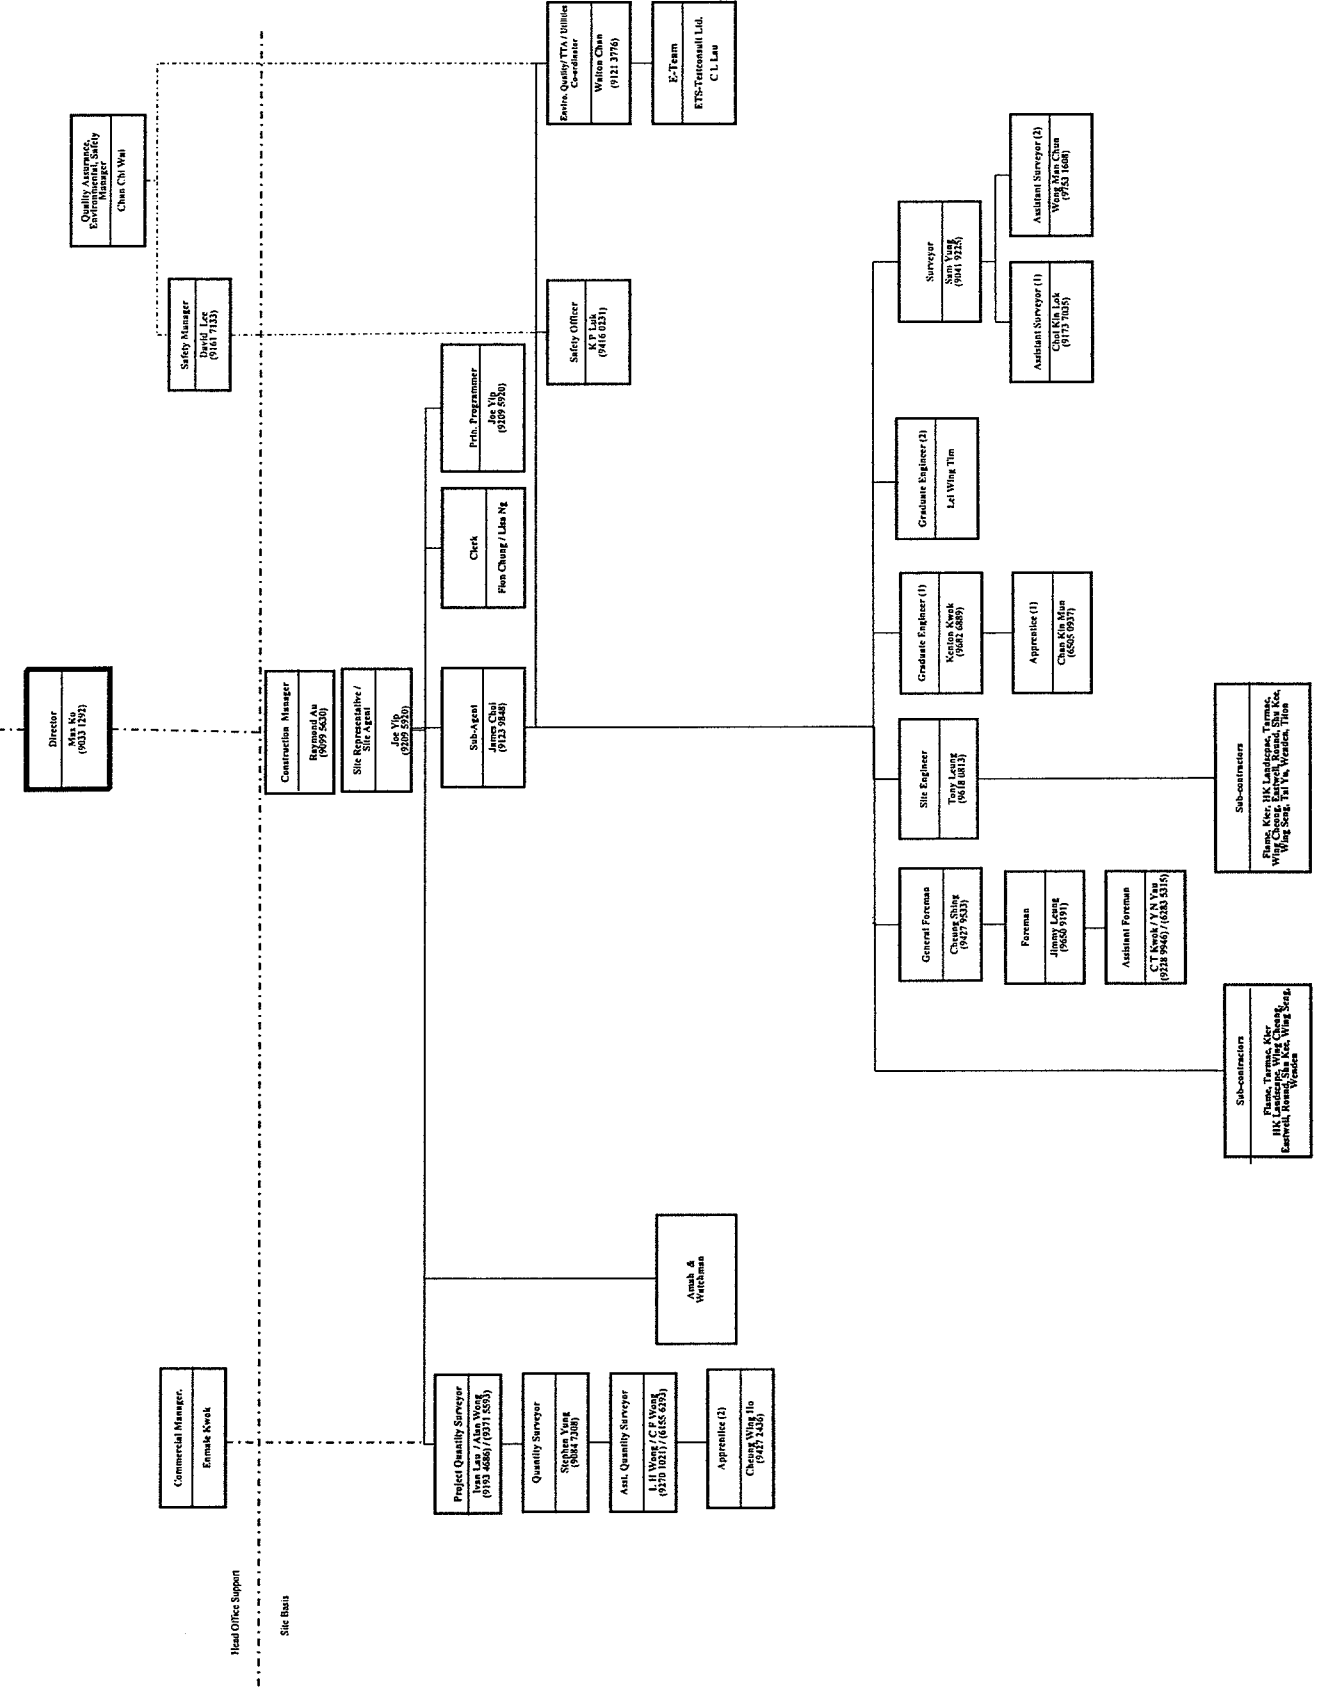


Lines of Communication

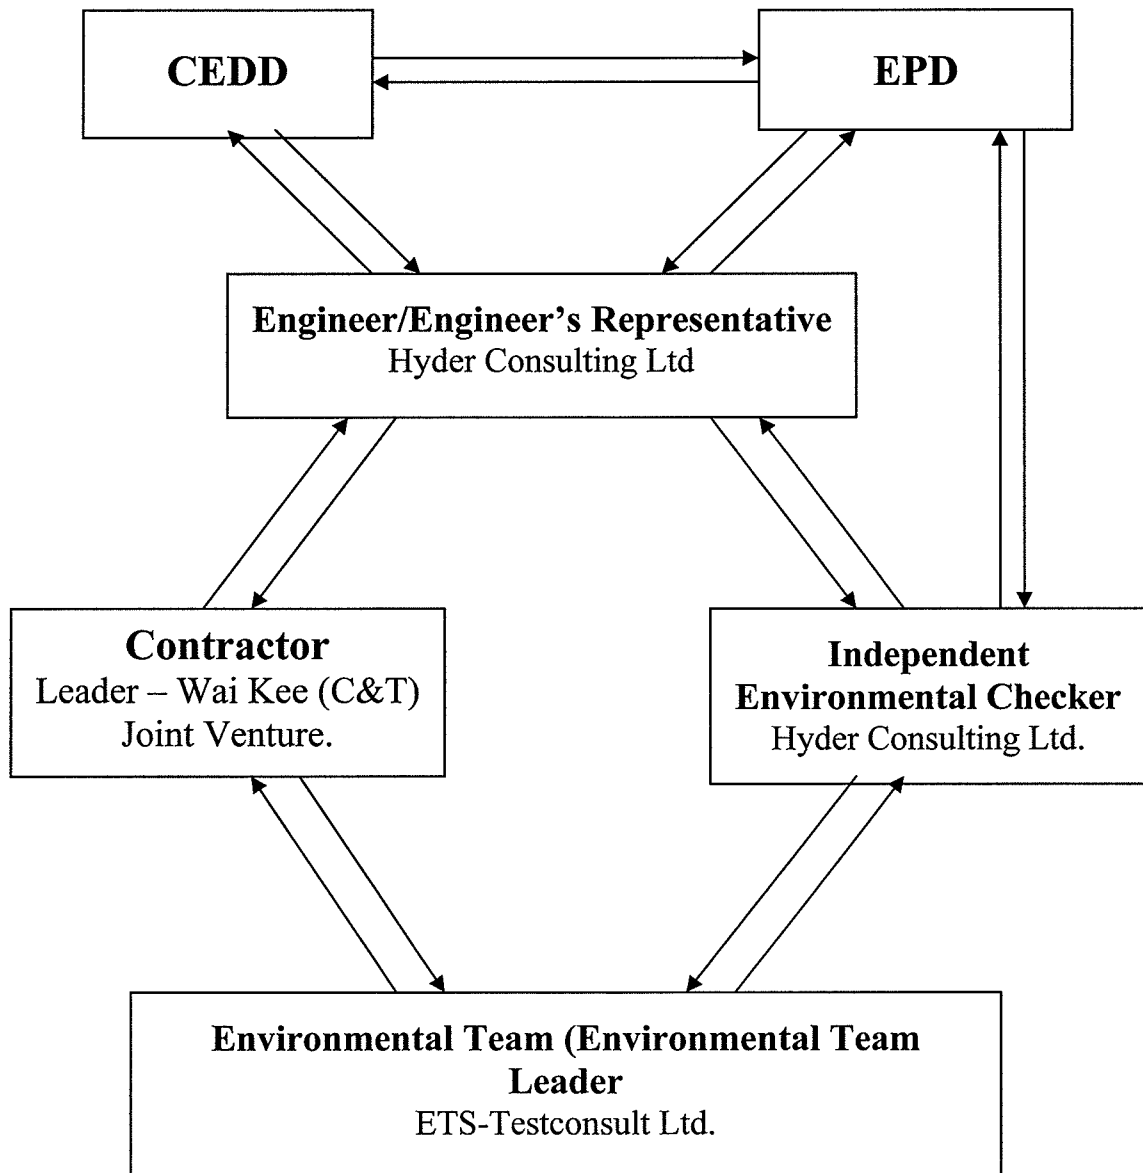



Appendix B1

Calibration Certificates for Air Quality Monitoring Equipments



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong

Tel : 2695 8318

E-mail : etl@ets-testconsult.com

Fax : 2695 3944

Web site : www.ets-testconsult.com

TEST REPORT

Calibration Report
of
High Volume Air Sampler

Manufacturer : Graseby GMW Date of Calibration : 22 January 2008


Serial No. : 1178 (ET / EA / 003 / 01) Calibration Due Date : 21 March 2008

Method : Based on Operations Manual for in series calibration method by TISCH
ENVIROMENTAL Model Te-5025A calibration kit

Results :

Flow recorder reading (cfm)	52	46	40	31	24
Qstd (Actual flow rate, m ³ /min)	1.71	1.52	1.33	1.06	0.83
Pressure :	768.81 mm Hg			Temp. :	293 K

Sampler 1178 Calibration Curve
Site: Pak Shek Kok (AM-1)
Date of Calibration: 22 January 2008

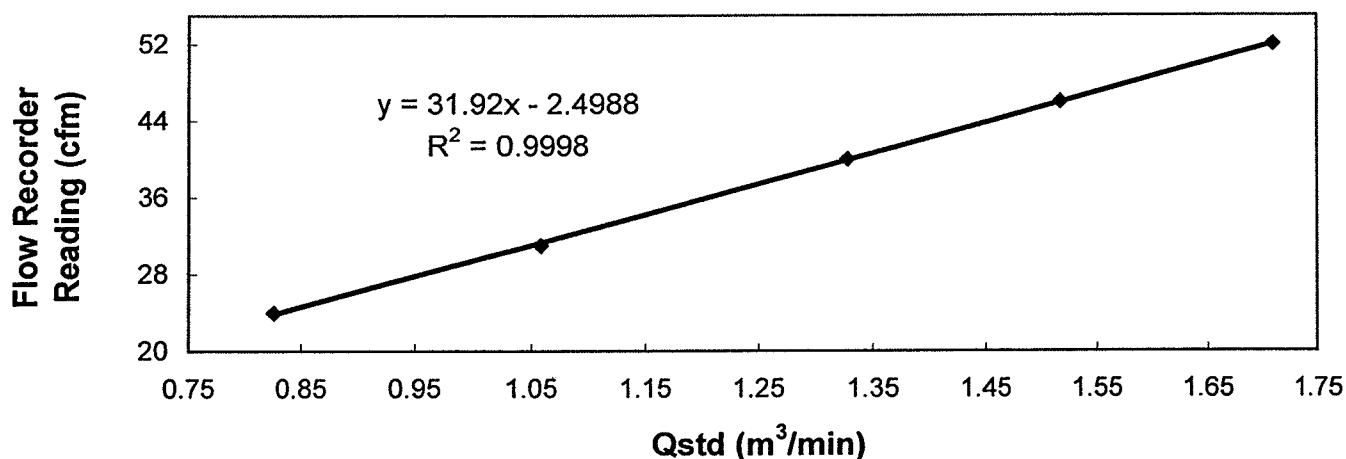


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies * / does not comply * with the specified requirements and is deemed acceptable * / unacceptable * for use.

Calibrated by : MAK Kei Wai
MAK Kei Wai
(Senior Technician)

Approved by : H. T. CHOW
H. T. CHOW
(Asst. Environmental Officer)



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong
Tel : 2695 8318 E-mail : etl@ets-testconsult.com
Fax : 2695 3944 Web site : www.ets-testconsult.com

TEST REPORT


**Calibration Report
of
High Volume Air Sampler**

Manufacturer : Graseby GMW **Date of Calibration** : 25 March 2008
Serial No. : 1178 (ET / EA / 003 / 01) **Calibration Due Date** : 24 May 2008
Method : Based on Operations Manual for in series calibration method by TISCH
ENVIROMENTAL Model Te-5025A calibration kit

Results :

Flow recorder reading (cfm)	52	46	39	30	23
Qstd (Actual flow rate, m ³ /min)	1.71	1.51	1.33	1.06	0.85
Pressure :	763.56 mm Hg			Temp. :	292 K

**Sampler 1178 Calibration Curve
Site: Pak Shek Kok (AM-1)
Date of Calibration: 25 March 2008**

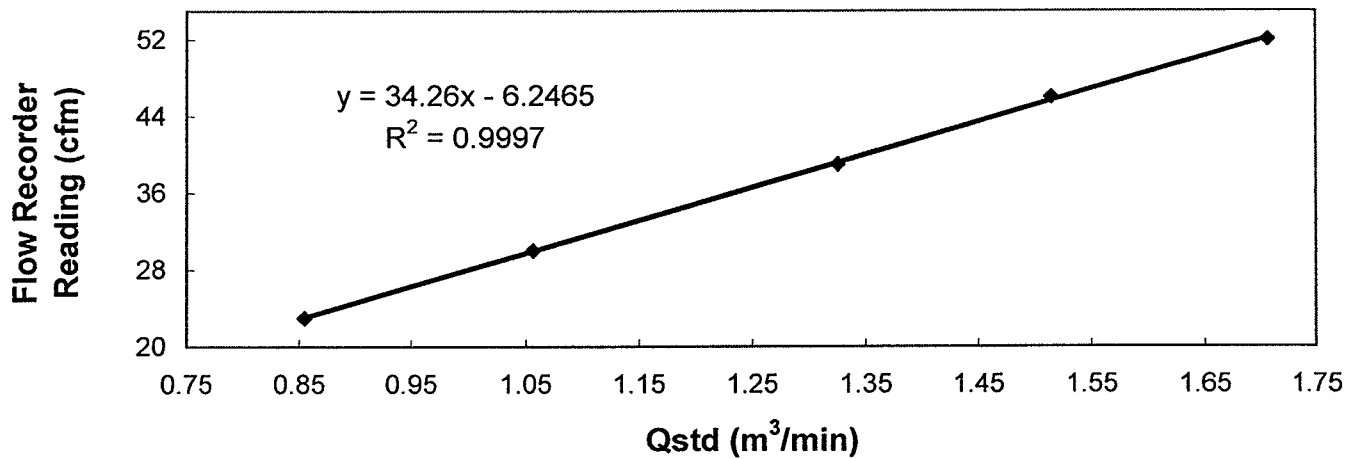


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies * / does not comply * with the specified requirements and is deemed acceptable * / unacceptable * for use.

Calibrated by :
CHOW, Hoi Tat
(Asst. Environmental Officer)

Approved by :
LAW, Sau Yee
(Senior Environmental Officer)



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong
Tel : 2695 8318 E-mail : etl@ets-testconsult.com
Fax : 2695 3944 Web site : www.ets-testconsult.com

TEST REPORT


**Calibration Report
of
High Volume Air Sampler**

Manufacturer : Graseby GMW **Date of Calibration** : 22 January 2008
Serial No. : 7179 (ET / EA / 003 / 16) **Calibration Due Date** : 21 March 2008
Method : Based on Operations Manual for in series calibration method by TISCH
ENVIROMENTAL Model Te-5025A calibration kit

Results :

Flow recorder reading (cfm)	51	46	41	32	25
Qstd (Actual flow rate, m ³ /min)	1.57	1.44	1.25	1.01	0.79
Pressure :	768.81 mm Hg			Temp. :	293 K

**Sampler 7179 Calibration Curve
Site: Pak Shek Kok (AM-3A)
Date of Calibration: 22 January 2008**

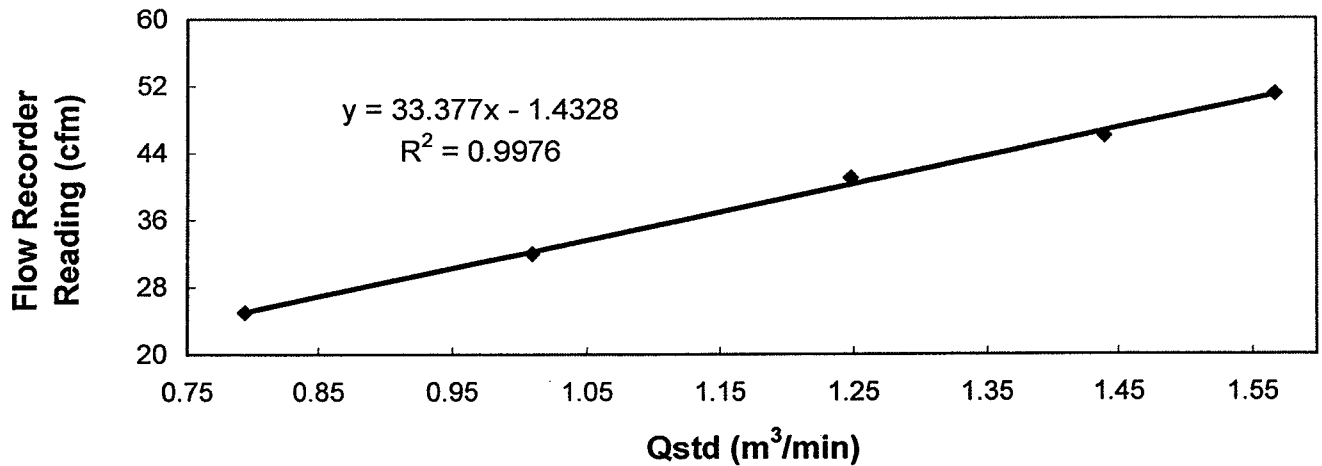


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies * / does not comply * with the specified requirements and is deemed acceptable * / unacceptable * for use.

Calibrated by : MAK Kei Wai
MAK Kei Wai
(Senior Technician)

Approved by : H. T. CHOW
H. T. CHOW
(Asst. Environmental Officer)



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong
Tel : 2695 8318 E-mail : etl@ets-testconsult.com
Fax : 2695 3944 Web site : www.ets-testconsult.com

TEST REPORT


Calibration Report
of
High Volume Air Sampler

Manufacturer : Graseby GMW Date of Calibration : 25 March 2008
Serial No. : 7179 (ET / EA / 003 / 16) Calibration Due Date : 24 May 2008
Method : Based on Operations Manual for in series calibration method by TISCH
ENVIROMENTAL Model Te-5025A calibration kit

Results :

Flow recorder reading (cfm)	52	47	40	32	24
Qstd (Actual flow rate, m ³ /min)	1.56	1.44	1.25	1.01	0.79
Pressure :	763.56 mm Hg			Temp. :	292 K

Sampler 7179 Calibration Curve
Site: Pak Shek Kok (AM-3A)
Date of Calibration: 25 March 2008

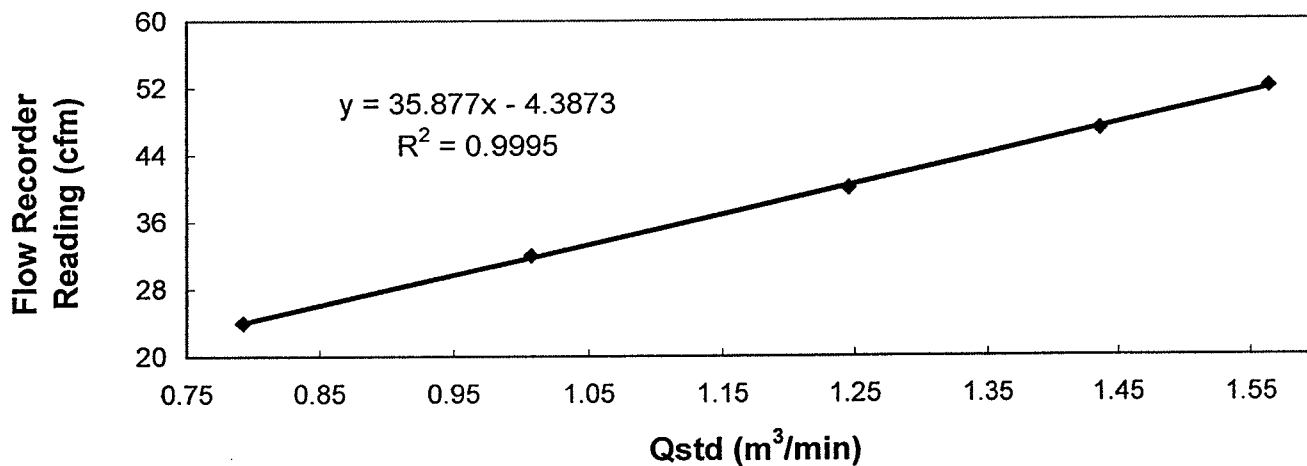

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies * / does not comply * with the specified requirements and is deemed acceptable * / unacceptable * for use.

Calibrated by :
CHOW, Hoi Tat
(Asst. Environmental Officer)

Approved by :
LAW, Sau Yee
(Senior Environmental Officer)



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong
Tel : 2695 8318 E-mail : etl@ets-testconsult.com
Fax : 2695 3944 Web site : www.ets-testconsult.com


TEST REPORT

**Calibration Report
of
High Volume Air Sampler**

Manufacturer : Graseby GMW **Date of Calibration** : 22 January 2008
Serial No. : 1172 (ET / EA / 003 / 11) **Calibration Due Date** : 21 March 2008
Method : Based on Operations Manual for in series calibration method by TISCH
ENVIROMENTAL Model Te-5025A calibration kit

Results :	Flow recorder reading (cfm)	60	55	49	41	33
	Qstd (Actual flow rate, m ³ /min)	1.63	1.47	1.28	1.02	0.81
	Pressure : 768.81 mm Hg	Temp. : 293 K				

**Sampler 1172 Calibration Curve
Site: Pak Shek Kok (AM-5)
Date of Calibration: 22 January 2008**

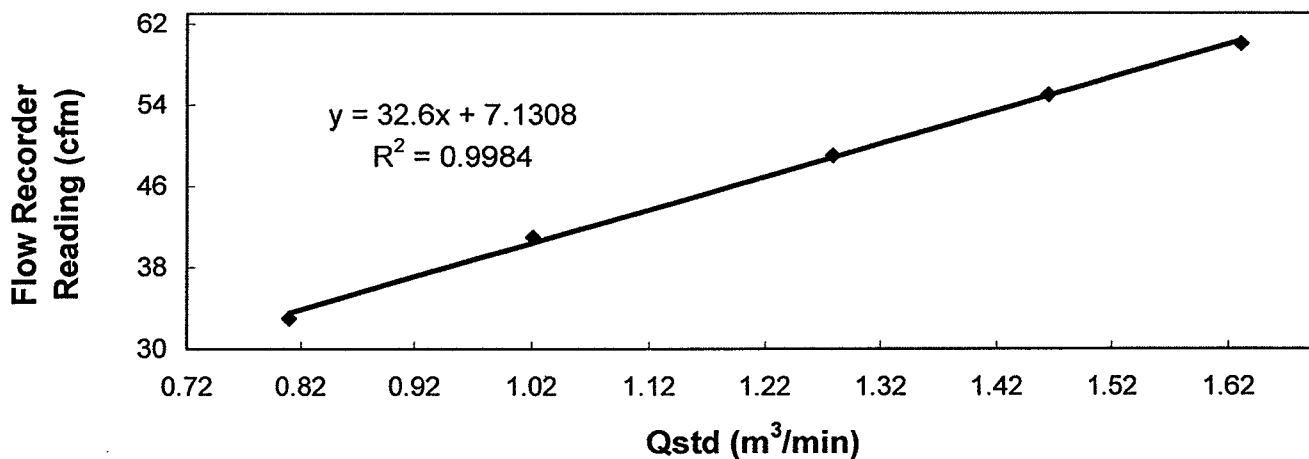


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies * / ~~does not comply~~ * with the specified requirements and is deemed acceptable * / unacceptable * for use.

Calibrated by : MAK Kei Wai
MAK Kei Wai
(Senior Technician)

Approved by : H. T. CHOW
H. T. CHOW
(Asst. Environmental Officer)



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F, Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong
Tel : 2695 8318 E-mail : etl@ets-testconsult.com
Fax : 2695 3944 Web site : www.ets-testconsult.com

TEST REPORT


**Calibration Report
of
High Volume Air Sampler**

Manufacturer : Graseby GMW Date of Calibration : 25 March 2008
Serial No. : 1172 (ET / EA / 003 / 11) Calibration Due Date : 24 May 2008
Method : Based on Operations Manual for in series calibration method by TISCH
ENVIROMENTAL Model Te-5025A calibration kit

Results :

Flow recorder reading (cfm)	60	55	49	40	33
Qstd (Actual flow rate, m ³ /min)	1.63	1.46	1.28	1.02	0.81
Pressure :	763.56 mm Hg			Temp. : 292 K	

**Sampler 1172 Calibration Curve
Site: Pak Shek Kok (AM-5)
Date of Calibration: 25 March 2008**

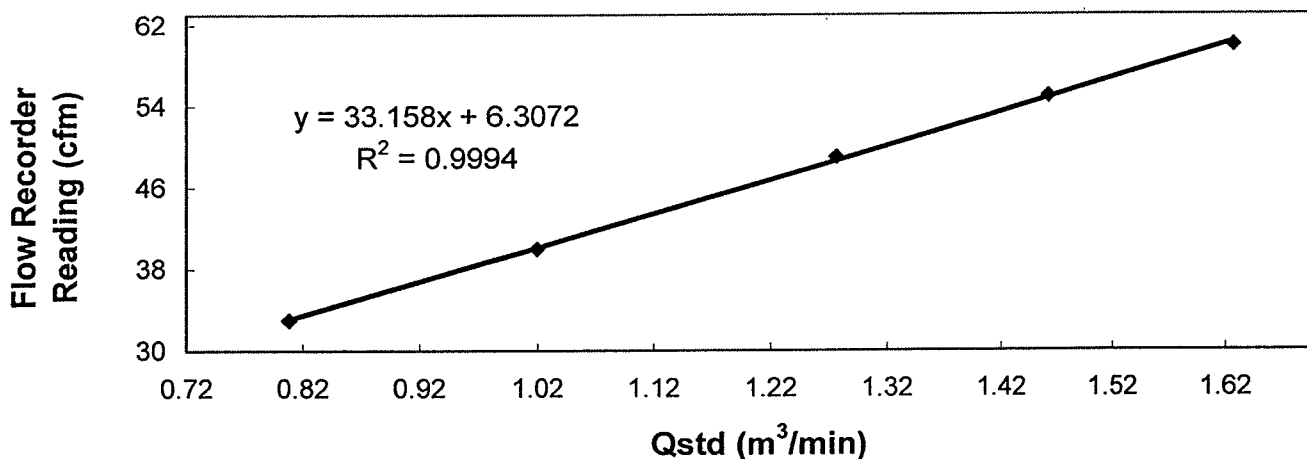


Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a 5-point calibration

The high volume sampler complies * / does not comply * with the specified requirements and is deemed acceptable * / unacceptable * for use.

Calibrated by :
CHOW, Hoi Tat
(Asst. Environmental Officer)

Approved by :
LAW, Sau Yee
(Senior Environmental Officer)



東業德勤測試顧問有限公司
ETS-TESTCONSULT LIMITED

8/F, Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan Street, Fotan, Hong Kong
Tel : 2695 8318 E-mail : etl@ets-testconsult.com
Fax : 2695 3944 Web site : www.ets-testconsult.com

TEST REPORT


Internal Calibration Report
of
Dust Trak Monitor

Manufacturer : TSI - 8520 Dust Trak Date of Calibration : 12 January 2008

Serial No. : 14230 (ET/EA/001/04) Due Date : 11 July 2008


Method : Parallel measurement (five-point calibration) by placing the Dust Trak Monitor and High Volume Air Samper together under the same environmental condition


Results	Dust Trak Monitor (ug/m ³)	44	64	119	202	247
	High Volume Air Sampler (ug/m ³)	32	41	96	170	225
	High Volume Air Sampler Serail No.: 1178	Calibration Due Date: 20 January 2008				

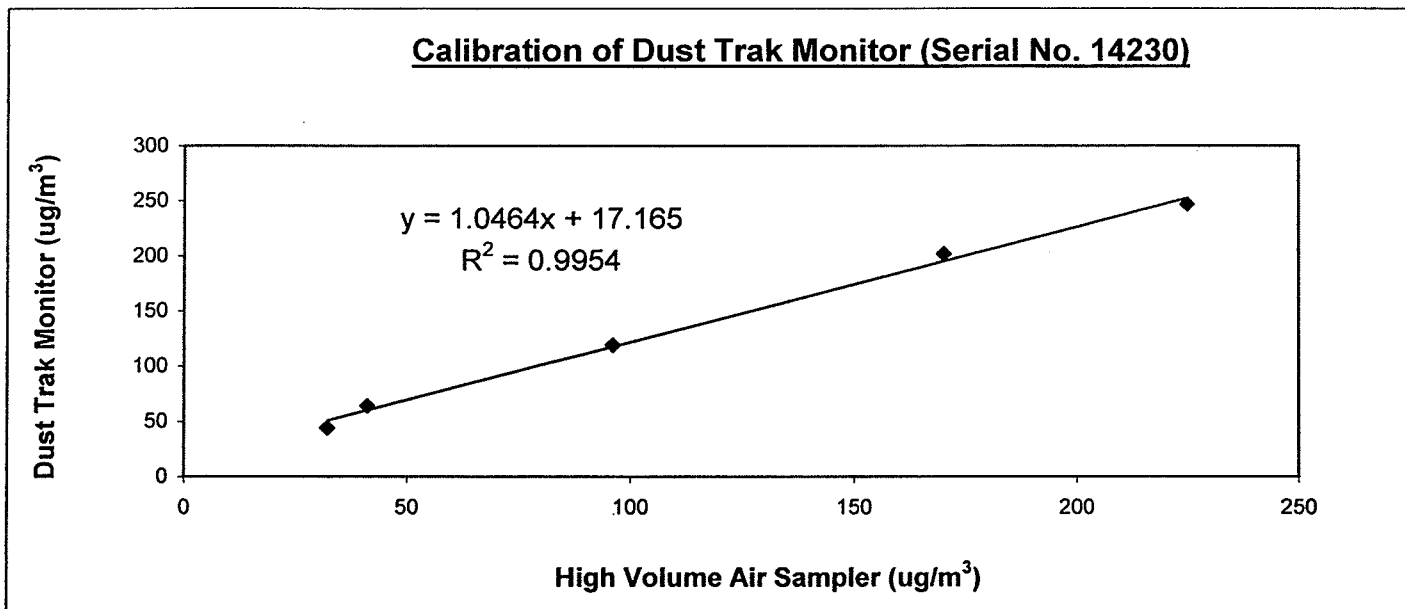

Acceptance Criteria : Correlation coefficient (r) of the calibration curve greater than 0.990 after a five point calibration

The Dust Trak Monitor complies * / does not comply * with the internal calibration procedures and is deemed acceptable * / unacceptable * for use.

Calibrated by : 
LEUNG, Ka Chun
(Assistant Environmental Officer)

Approved by : 
LAW, Sau Yee
(Senior Environmental Officer)

Appendix B2

Air Quality Monitoring Results

Summary of 24-hr TSP Monitoring Results

Monitoring Station : AM1
Location : HKIB Staff Accommodation

Start Date	Time	Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Weight (g)		Conc. (µg/m ³)	Weather Condition
		Date	Time	Initial	Final		Initial	Final		Initial	Final		
06/03/08	09:10	07/03/08	08:30	12748.00	12771.33	23.33	1.1121	1.1121	1.1121	2.8469	2.9896	92	Cloudy
12/03/08	10:55	13/03/08	09:54	12771.33	12794.32	22.99	1.0495	1.0495	1.0495	2.8714	2.9597	61	Sunny
18/03/08	11:07	19/03/08	10:22	12794.32	12817.57	23.25	1.1434	1.1434	1.1434	2.7905	2.9363	91	Cloudy
25/03/08	08:42	26/03/08	08:16	12817.57	12841.14	23.57	1.2331	1.2331	1.2331	2.8026	2.9888	107	Cloudy
31/03/08	14:30	01/04/08	14:05	12841.14	12864.73	23.58	1.2331	1.2331	1.2331	2.8855	2.9474	35	Cloudy

Monitoring Station : AM3A
Location : Cheung Shue Tan (in front of Man Kee Store)

Start Date	Time	Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Weight (g)		Conc. (µg/m ³)	Weather Condition
		Date	Time	Initial	Final		Initial	Final		Initial	Final		
06/03/08	08:40	07/03/08	08:32	18220.11	18243.98	23.87	1.0616	1.0616	1.0616	2.8858	3.0171	86	Cloudy
12/03/08	10:24	13/03/08	10:24	18243.98	18267.98	24.00	1.1515	1.1515	1.1515	2.8011	2.9102	66	Sunny
18/03/08	13:10	19/03/08	12:22	18267.98	18291.18	23.20	1.1515	1.1515	1.1515	2.8873	3.0620	109	Cloudy
25/03/08	08:15	26/03/08	08:15	18291.18	18315.18	24.00	1.1515	1.1515	1.1515	2.8234	2.9710	89	Cloudy
31/03/08	11:05	01/04/08	11:05	18315.18	18339.18	24.00	1.1536	1.1536	1.1536	2.8765	2.9247	29	Cloudy

Monitoring Station : AM5
Location : Wen Chih Tang at the CUHK

Start Date	Time	Finish		Elapse Time		Sampling Time (hrs)	Flow Rate (m ³ /min.)		Average (m ³ /min.)	Filter Weight (g)		Conc. (µg/m ³)	Weather Condition
		Date	Time	Initial	Final		Initial	Final		Initial	Final		
06/03/08	09:00	07/03/08	08:28	8122.74	8146.21	23.47	0.9162	0.9162	0.9162	2.8383	2.9448	83	Cloudy
12/03/08	10:38	13/03/08	10:10	8146.21	8169.75	23.54	0.8242	0.8242	0.8242	2.8333	2.8949	53	Sunny
18/03/08	15:40	19/03/08	15:32	8169.75	8193.61	23.86	0.8242	0.8242	0.8242	2.8762	2.9853	92	Cloudy
25/03/08	08:35	26/03/08	08:39	8193.61	8217.68	24.07	0.9352	0.9352	0.9352	2.8137	2.9397	104	Cloudy
31/03/08	13:15	01/04/08	12:28	8217.68	8240.89	23.21	0.8352	0.8352	0.8352	2.8977	2.9369	34	Cloudy

Summary of 1-hr TSP Monitoring Results

Monitoring Station : AM1 (HKIB Staff Accommodation)

Date	Monitoring Period		1-hr TSP ($\mu\text{g}/\text{m}^3$)			Weather
	Start	Finish	Minimum	Maximum	Average	
01/03/08	10:00	11:00	101	415	115	Sunny
04/03/08	13:02	14:02	78	420	158	Sunny
06/03/08	15:00	16:00	101	402	116	Cloudy
08/03/08	13:00	14:00	64	519	188	Sunny
11/03/08	08:30	09:30	98	447	136	Cloudy
12/03/08	13:00	14:00	61	522	208	Sunny
13/03/08	08:30	09:30	97	437	125	Cloudy
15/03/08	11:00	12:00	54	494	198	Sunny
18/03/08	11:00	12:00	98	449	134	Cloudy
19/03/08	17:00	18:00	57	463	196	Sunny
20/03/08	09:15	10:15	42	448	182	Cloudy
25/03/08	18:00	19:00	41	423	159	Cloudy
27/03/08	18:00	19:00	49	464	190	Cloudy
29/03/08	13:00	14:00	70	341	134	Sunny
31/03/08	14:25	15:25	49	425	170	Cloudy

Monitoring Station : AM3 – Cheung Shue Tan in front of Man Kee Store

Date	Monitoring Period		1-hr TSP ($\mu\text{g}/\text{m}^3$)			Weather
	Start	Finish	Minimum	Maximum	Average	
01/03/08	13:00	14:00	64	342	77	Sunny
04/03/08	15:20	16:20	60	345	99	Sunny
06/03/08	16:20	17:20	74	337	83	Cloudy
08/03/08	15:30	16:30	51	450	139	Sunny
11/03/08	16:15	17:15	73	359	97	Cloudy
12/03/08	09:15	10:15	43	424	145	Sunny
13/03/08	16:40	17:40	65	359	81	Cloudy
15/03/08	14:15	15:15	42	375	141	Sunny
18/03/08	13:00	14:00	74	363	97	Cloudy
19/03/08	14:30	15:30	41	393	143	Sunny
20/03/08	14:15	15:15	36	329	132	Cloudy
25/03/08	15:45	16:45	33	339	126	Cloudy
27/03/08	13:00	14:00	35	357	126	Cloudy
29/03/08	08:45	09:45	50	298	99	Sunny
31/03/08	11:00	12:00	33	326	123	Cloudy

Summary of 1-hr TSP Monitoring Results

Monitoring Station : AM5 - Near Wen Chih Tang at the CUHK

Date	Monitoring Period		1-hr TSP ($\mu\text{g}/\text{m}^3$)			Weather
	Start	Finish	Minimum	Maximum	Average	
01/03/08	14:20	15:20	77	379	95	Sunny
04/03/08	14:08	15:08	70	388	95	Sunny
06/03/08	17:35	18:35	81	343	96	Cloudy
08/03/08	14:15	15:15	56	462	154	Sunny
11/03/08	17:30	18:30	80	372	106	Cloudy
12/03/08	10:30	11:30	54	496	173	Sunny
13/03/08	17:55	18:55	83	370	102	Cloudy
15/03/08	13:00	14:00	48	408	166	Sunny
18/03/08	15:30	16:30	80	375	99	Cloudy
19/03/08	15:45	16:45	49	408	160	Sunny
20/03/08	13:00	14:00	39	353	148	Cloudy
25/03/08	16:55	17:55	39	367	133	Cloudy
27/03/08	16:50	17:50	41	398	163	Cloudy
29/03/08	14:15	15:15	61	328	117	Sunny
31/03/08	13:10	14:10	41	384	146	Cloudy




Appendix B3


Graphical Plots of Air Quality Monitoring Data




1-hour TSP level at AM1, HKIB Staff Accommodation

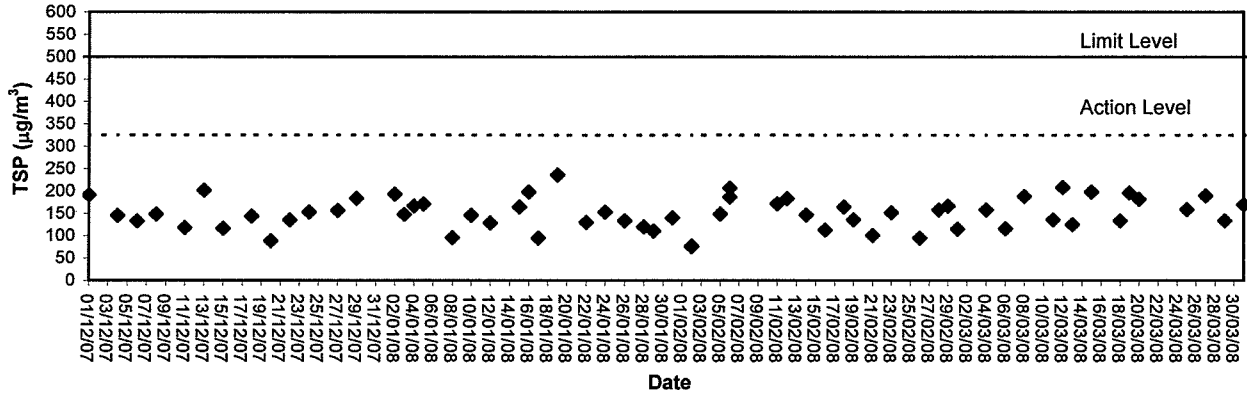

1-hour TSP level at AM3, Cheung Shue Tan Village (near the outer building, a temple)

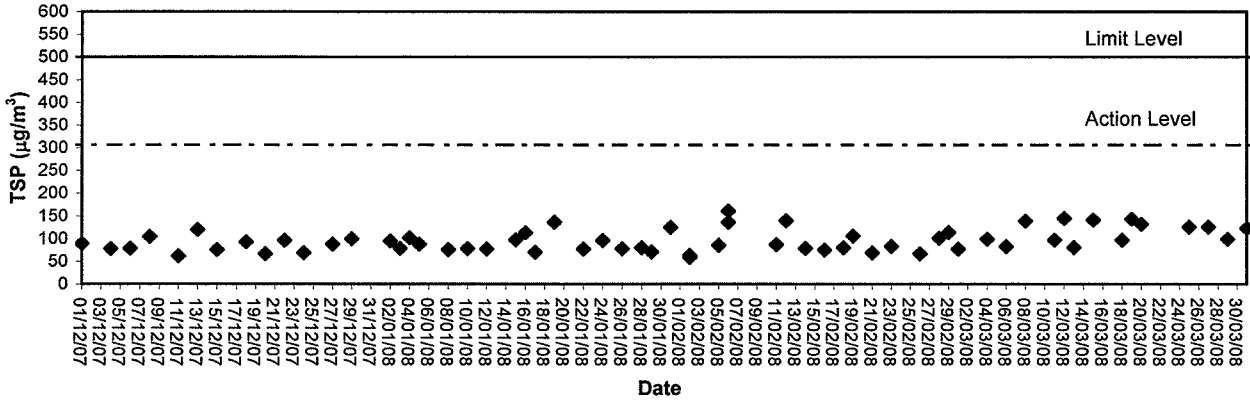


1-hour TSP level at AM5 Wen Chih Tang at the CUHK

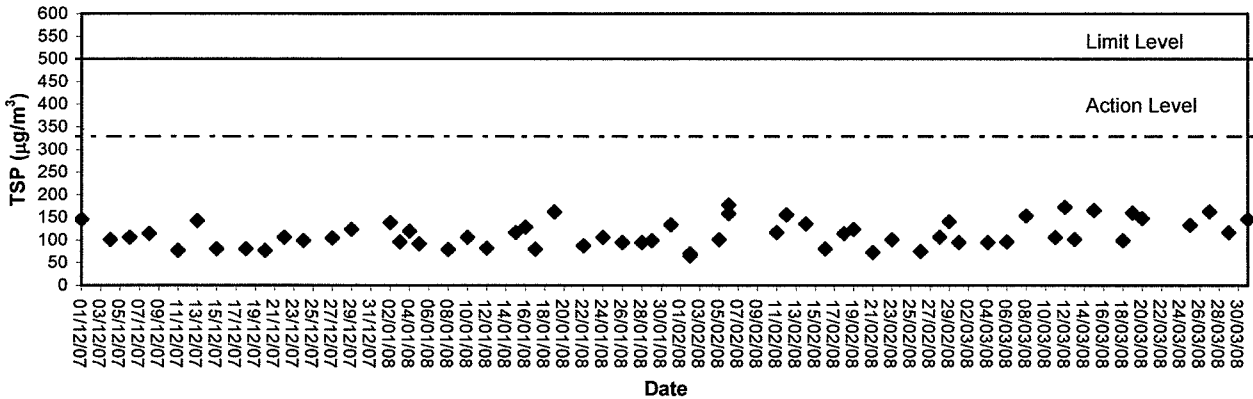





24-hour TSP level at AM1 (HKIB Staff Accommodation)

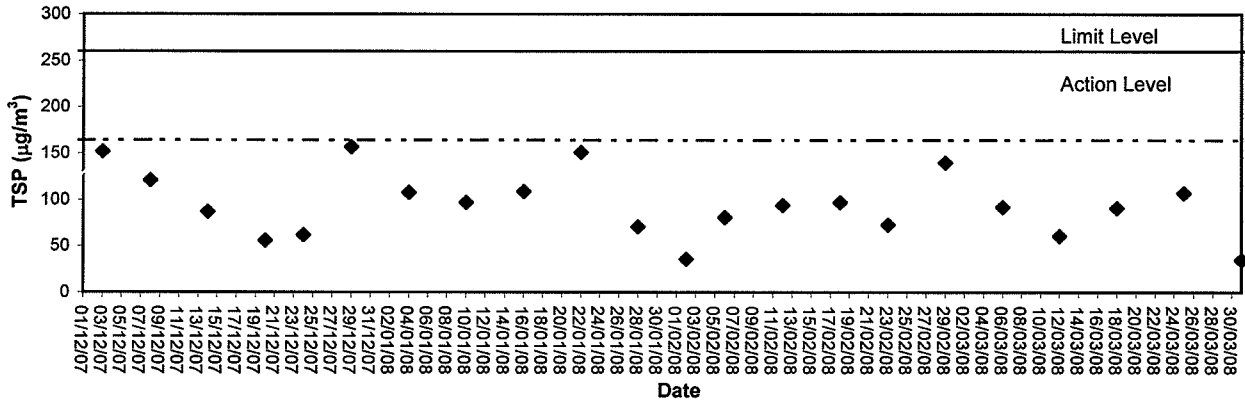

24-hour TSP level at AM3A (Cheung Shue Tan in front of Man Kee Store)

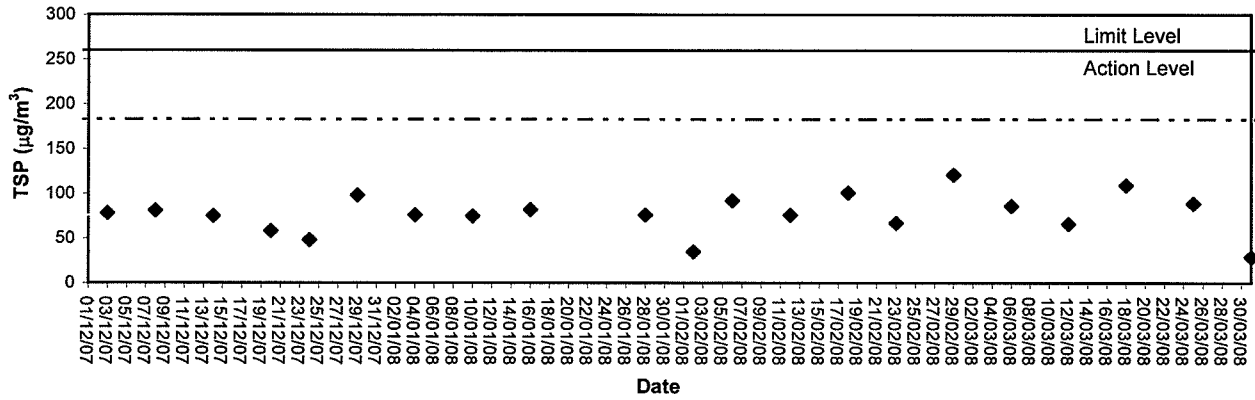

24-hour TSP level at AM5 (Wen Chih Tang at the CUHK)

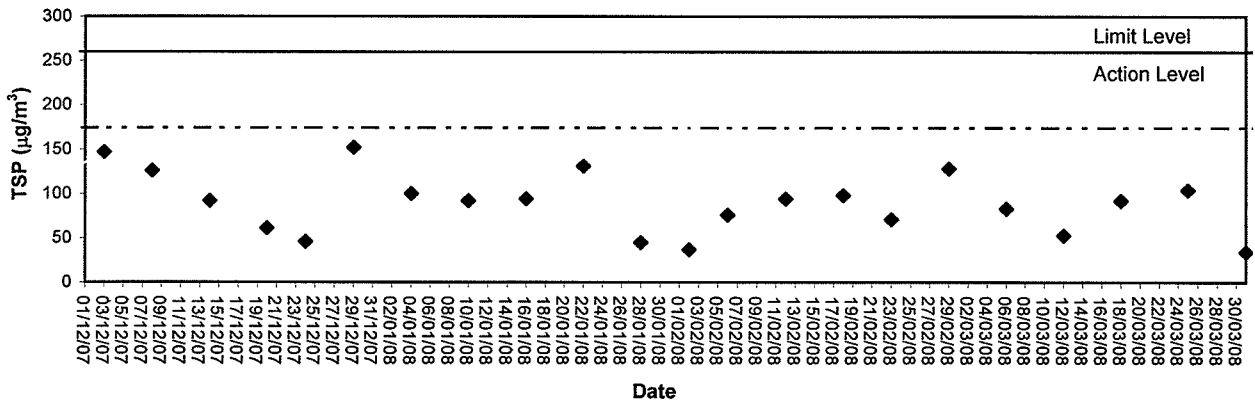



Appendix C1

Calibration Certificates for Noise Monitoring Equipments



Hong Kong Calibration Ltd.

香港校正有限公司

Calibration Certificate

Certificate No. 71392A

Page 1 of 2 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q70569

Date of receipt : 30-Mar-07

Item Tested

Description : Sound Level Calibrator

Manufacturer : Rion

Model : NC-73

Serial No. : 10644871

Test Conditions

Date of Test : 17-Apr-07

Supply Voltage : -

Ambient Temperature : (23 ± 3)°C

Relative Humidity : (50 ± 25) %

Test Specifications

Calibration check.

Calibration procedure : F21, Z02.

Test Results

All results were within the manufacturer's specification.

The results are shown in the attached page(s).


Main Test equipment used:


<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Due Date</u>	<u>Traceable to</u>
S014	Spectrum Analyzer	62914	7-Jul-07	NIM-PRC & SCL-HKSAR
S024	Sound Level Calibrator	62691	22-Apr-07	NIM-PRC & SCL-HKSAR
S041	Universal Counter	63839	22-Aug-07	SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI).

The test results apply to the above Unit-Under-Test only

Calibrated by : 
P.F. Wong

Approved by : 
Dorothy Cheuk

Date: 2-May-07

This Certificate is issued by:
Hong Kong Calibration Ltd.
Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.
Tel: 2425 8801 Fax: 2425 8846

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full.



Calibration Certificate

Certificate No. 71392A

Page 2 of 2 Pages

Results :

1. Level Accuracy (at 1 kHz)

UUT Nominal Value	Measured Value	Mfr's Spec.
94 dB	93.96 dB	± 1 dB

Uncertainty : ± 0.1 dB

2. Frequency Accuracy

UUT Nominal Value	Measured Value	Mfr's Spec.
1 kHz	0.981 kHz	± 2 %

Uncertainty : ± 0.1 %

3. Level Stability : 0.1 dB

Uncertainty : ± 0.01 dB

4. Total Harmonic Distortion : < 1.0 %

Mfr's Spec. : < 3 %

Uncertainty : ± 2.3 % of reading

Remark : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. The above measured values are the mean of 3 measurement.

4. Atmospheric Pressure : 990hPa

5. This certificate is to supercede our former certificate no. : 71392

----- END -----



Calibration Certificate

Certificate No. 71391

Page 1 of 3 Pages

Customer : ETS-Testconsult Limited

Address : 8/F., Block B, Veristrong Industrial Centre, 34-36 Au Pui Wan St., Fotan, Hong Kong.

Order No. : Q70569

Date of receipt : 30-Mar-07

Item Tested

Description : Precision Integrating Sound Level Meter

Manufacturer : Rion

Model : NL-31

Serial No. : 00110024

Test Conditions

Date of Test : 17-Apr-07

Supply Voltage : -

Ambient Temperature : (23 ± 3)°C

Relative Humidity : (50 ± 25) %

Test Specifications

Calibration check.

Calibration procedure : Z01.

Test Results

All results were within the IEC 651 Type 1 & IEC 804 Type 1 specification.

The results are shown in the attached page(s).


Main Test equipment used:


<u>Equipment No.</u>	<u>Description</u>	<u>Cert. No.</u>	<u>Due Date</u>	<u>Traceable to</u>
S017	Multi-Function Generator	C071115	14-Mar-08	SCL-HKSAR
S024	Sound Level Calibrator	62691	22-Apr-07	NIM-PRC & SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI).

The test results apply to the above Unit-Under-Test only

Calibrated by : 
P.F. Wong

Approved by : 
Dorothy Cheuk

Date: 17-Apr-07

This Certificate is issued by:

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong.

Tel: 2425 8801 Fax: 2425 8646



Calibration Certificate

Certificate No. 71391

Page 2 of 3 Pages

Results :

1. SPL Accuracy

UUT Setting			Applied Value (dB)	UUT Reading (dB)
Level Range (dB)	Weight	Response		
20 - 100	L _A	Fast	94.07	94.0
		Slow		94.0
	L _C L _p	Fast		94.1
		Fast		94.1
30 - 120	L _A	Fast	94.07	94.0
		Slow		94.0
	L _C L _p	Fast		94.0
		Fast		94.1
30 - 120	L _A	Fast	113.95	113.9
		Slow		113.9
	L _C L _p	Fast		113.9
		Fast		114.0

IEC 651 Type 1 Spec. : ± 0.7 dB

Uncertainty : ± 0.1 dB

2. Level Stability : 0.0 dB

IEC 651 Type 1 Spec. : ± 0.3 dB

Uncertainty : ± 0.01 dB

3. Linearity

3.1 Level Linearity

UUT Range	Applied Value (dB)	UUT Rdg (dB)	Variation (dB)	IEC 651 Type 1 Spec. (inside Primary)
130	114.0	114.1	0.1	± 0.7 dB
130	104.0	104.0	0.0	
120	94.0	94.0 (Ref.)	0.0	
110	84.0	84.1	0.1	
100	74.0	74.1	0.1	
90	64.0	64.1	0.1	
80	54.0	54.1	0.1	

Uncertainty : ± 0.1 dB



Calibration Certificate

Certificate No. 71391

Page 3 of 3 Pages

3.2 Differential level linearity

UUT Range	Applied Value (dB)	UUT Rdg (dB)	Variation (dB)	IEC 651 Type 1 Spec.
120	84.0	84.0	0.0	± 0.4
	94.0	94.0 (Ref.)	--	
	95.0	95.0	0.0	± 0.2
	104.0	104.0	0.0	± 0.3
	105.0	105.0	0.0	± 1.0

Uncertainty : ± 0.1 dB

4. Frequency Weighting

A weighting

Frequency	Attenuation (dB)	IEC 651 Type 1 Spec.
31.5 Hz	- 39.6	- 39.4 dB, ± 1.5 dB
63 Hz	- 26.3	- 26.2 dB, ± 1.5 dB
125 Hz	- 16.2	- 16.1 dB, ± 1 dB
250 Hz	- 8.7	- 8.6 dB, ± 1 dB
500 Hz	- 3.3	- 3.2 dB, ± 1 dB
1 kHz	0.0 (Ref.)	0 dB, ± 1 dB
2 kHz	+ 1.3	+ 1.2 dB, ± 1 dB
4 kHz	+ 1.1	+ 1.0 dB, ± 1 dB
8 kHz	- 1.1	- 1.1 dB, + 1.5 dB ~ - 3 dB
16 kHz	- 6.7	- 6.6 dB, + 3 dB ~ ∞

Uncertainty : ± 0.1 dB

5. Time Averaging

Applied Burst duty Factor	Applied Leq Value (dB)	UUT Reading (dB)	IEC 804 Type 1 Spec.
continuous	40.0	40.0	--
1/10	40.0	39.9	± 0.5 dB
1/10 ²	40.0	40.0	
1/10 ³	40.0	39.9	± 1.0 dB
1/10 ⁴	40.0	39.9	

Uncertainty : ± 0.1 dB

Remark : 1. UUT : Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure : 990 hPa.

4. The internal cal reference of UUT was drifted from 94.0 dB to 93.4 dB.

----- END -----



Appendix C2

Noise Monitoring Results

Day-time Noise Monitoring

Monitoring Location: NM1 (HKIB Staff Accommodation)

Date	Start Sampling Time (hh:mm)	Noise Level dB (A)			Wind Speed (m/s)	Weather Condition
		L _{eq(30min)}	L10	L90		
04/03/08	13:08	59.4	62.5	56.5	1.2	Sunny
11/03/08	08:35	57.9	60.2	55.6	1.0	Cloudy
18/03/08	11:02	57.8	60.3	55.9	0.9	Cloudy
25/03/08	18:05	67.9	72.2	64.0	1.5	Cloudy

Monitoring Location: NM2 (CUHK Residence No.10)

Date	Start Sampling Time (hh:mm)	Noise Level dB (A)			Wind Speed (m/s)	Weather Condition
		L _{eq(30min)}	L10	L90		
04/03/08	13:50	57.1	59.9	54.4	1.1	Sunny
11/03/08	09:15	55.6	58.2	51.6	1.1	Cloudy
18/03/08	14:15	56.0	59.1	53.6	0.7	Cloudy
25/03/08	16:15	56.8	59.3	53.8	0.7	Cloudy

Mon Monitoring Location: NM3 (Cheung Shue Tan Village)

Date	Start Sampling Time (hh:mm)	Noise Level dB (A)			Wind Speed (m/s)	Weather Condition
		L _{eq(30min)}	L10	L90		
04/03/08	15:22	50.7	53.6	48.7	0.5	Sunny
11/03/08	16:20	52.0	54.7	49.1	0.8	Cloudy
18/03/08	13:02	52.2	54.6	49.4	1.2	Cloudy
25/03/08	15:30	53.7	57.0	51.2	0.6	Cloudy

Monitoring Location: NM8 (Near Wen Chih Tang at the CUHK)

Date	Start Sampling Time (hh:mm)	Noise Level dB (A)			Wind Speed (m/s)	Weather Condition
		L _{eq(30min)}	L10	L90		
04/03/08	14:30	55.9	58.9	53.3	1.2	Sunny
11/03/08	17:35	54.8	57.3	51.8	0.9	Cloudy
18/03/08	15:32	54.2	56.6	51.8	1.1	Cloudy
25/03/08	17:10	57.0	59.9	54.0	1.1	Cloudy







Appendix C3

Graphical Plots of Noise Monitoring Data



Noise Monitoring (Day-time)

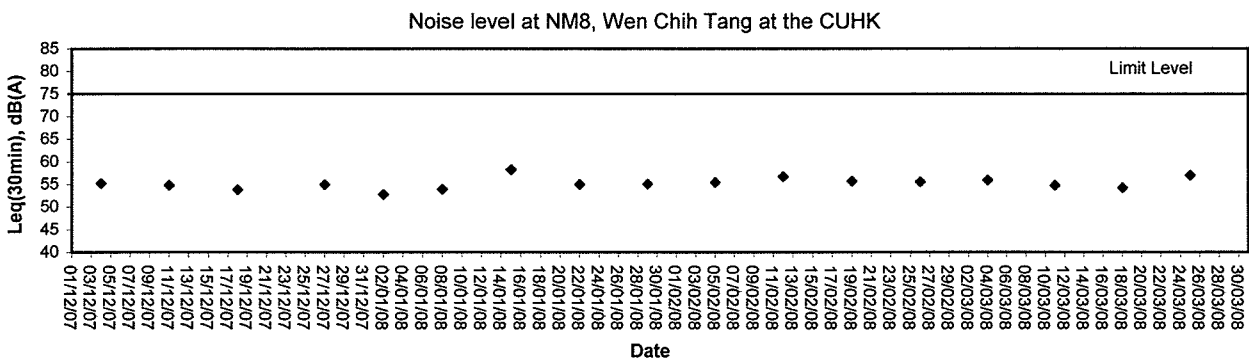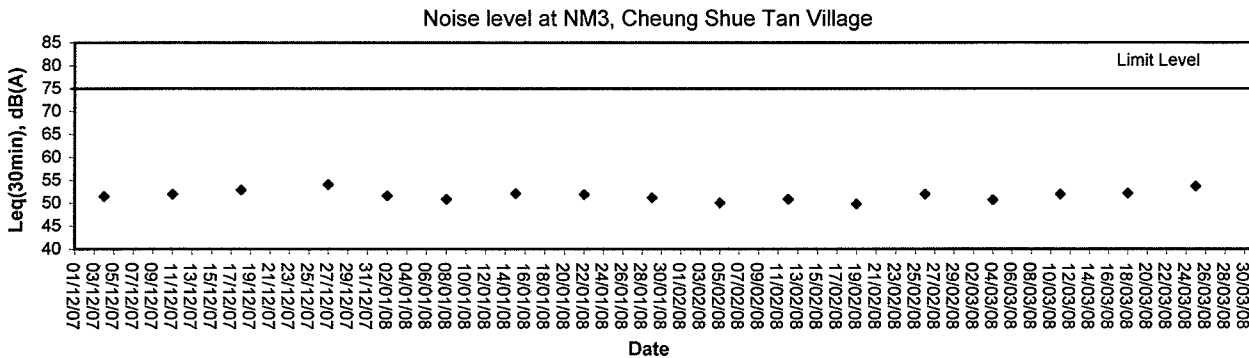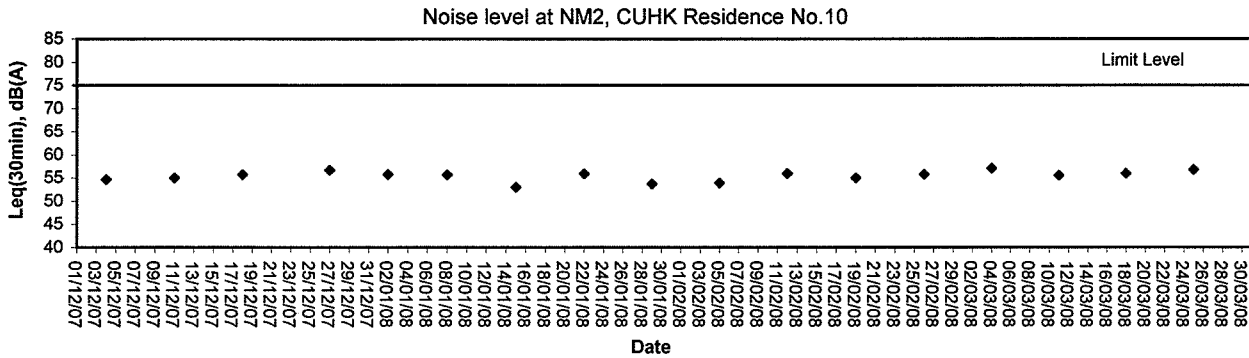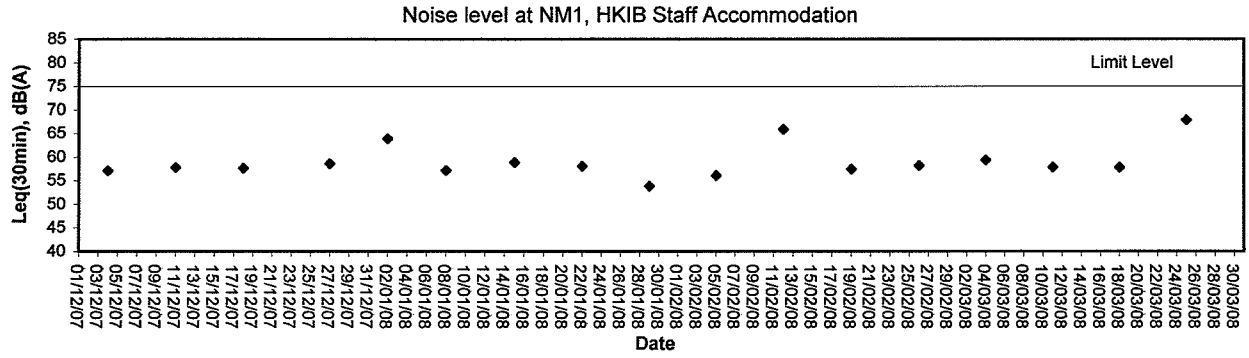



Appendix D

Weather Condition

Weather Condition

Date	Rainfall (mm)	Max. Temp (°C)	Min. Temp. (°C)	Relative Humidity (%)	Wind Direction	Wind Speed (m/s)
01/03/08	0.0	21.4	9.2	59	110	<5
02/03/08	0.0	25.0	9.5	63	230	<5
03/03/08	0.0	26.2	10.3	58	020	<5
04/03/08	0.0	23.3	11.1	57	090	<5
05/03/08	0.0	20.4	12.8	52	110	<5
06/03/08	0.0	21.0	12.4	59	340	<5
07/03/08	0.0	22.8	15.1	70	080	<5
08/03/08	0.0	24.2	15.3	66	110	<5
09/03/08	0.0	25.0	13.9	76	070	<5
10/03/08	0.0	23.8	15.9	72	100	<5
11/03/08	0.0	26.0	15.6	74	040	<5
12/03/08	0.0	23.2	16.1	78	130	<5
13/03/08	0.5	25.5	18.0	80	350	<5
14/03/08	0.0	24.6	19.2	75	070	<5
15/03/08	0.0	23.3	17.7	59	050	<5
16/03/08	0.0	25.6	18.0	72	360	<5
17/03/08	0.0	23.9	20.0	83	080	<5
18/03/08	0.0	24.5	19.6	86	060	<5
19/03/08	0.0	28.5	19.1	76	070	<5
20/03/08	0.5	21.1	18.9	73	080	<5
21/03/08	0.0	20.9	18.5	80	100	<5
22/03/08	37.5	21.2	19.7	89	060	<5
23/03/08	0.0	20.2	17.9	71	040	<5
24/03/08	0.0	24.4	16.3	67	080	<5
25/03/08	0.0	20.3	17.1	73	360	<5
26/03/08	10.5	20.2	14.7	84	360	<5
27/03/08	0.0	23.6	13.5	79	090	<5
28/03/08	11.5	24.8	21.2	84	220	<5
29/03/08	0.0	28.1	21.8	79	220	<5
30/03/08	0.0	26.6	21.4	88	050	<5
31/03/08	3.5	22.1	16.6	89	090	<5

Remark: Data of wind speed and wind direction were extracted from Hong Kong Observatory (Shatin Station).



Appendix E

Event-Action Plans



Event / Action Plan for Air Quality

EVENT	ET Leader	ACTION			CNTRACTOR
		IC(E)	ER		
<p>Action Level</p> <p>1. Exceedance of one sample</p> <p>2. Exceedance for two or more consecutive samples</p>	<p>1. Identify source</p> <p>2. Inform IC(E) and ER</p> <p>3. Repeat measurement to confirm finding</p> <p>4. Increase monitoring frequency to daily</p> <p>1. Identify source</p> <p>2. Inform IC(E) and ER</p> <p>3. Repeat measurement to confirm findings</p> <p>4. Increase monitoring frequency to daily</p> <p>5. Discuss with IC(E) and Contractor on remedial actions required</p> <p>6. If exceedance continuous, arrange meeting with IC(E) and ER</p> <p>7. If exceedance stops, cease additional monitoring</p>	<p>1. Check monitoring data submitted by ET</p> <p>2. Check Contractor's working method.</p> <p>1. Checking monitoring data submitted by ET</p> <p>2. Check Contractor's working method</p> <p>3. Discuss with ET and Contractor on possible remedial measures</p> <p>4. Advise the ER on the effectiveness of the proposed remedial measures</p> <p>5. Supervisor implementation of remedial measures</p>	<p>1. Notify Contractor</p> <p>1. Confirm receipt of notification of failure in writing</p> <p>2. Notify Contractor</p> <p>3. Ensure remedial measures properly implemented</p>	<p>1. Rectify any unacceptable practice</p> <p>2. Amend working methods if possible</p> <p>1. Submit proposals for remedial action to IC(E) within 3 working days of notification</p> <p>2. Implement the agreed proposals</p> <p>3. Amend proposal if possible</p>	
<p>Limit Level</p> <p>1. Exceedance of one sample</p> <p>2. Exceedance for two or more consecutive samples</p>	<p>1. Identify source</p> <p>2. Inform ER and EPD</p> <p>3. Repeat measurement to confirm finding</p> <p>4. Increase monitoring frequency to daily</p> <p>5. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results</p> <p>1. Notify IC(E), ER, Contractor and EPD</p> <p>2. Identify source</p> <p>3. Repeat measurement to confirm findings</p> <p>4. Increase monitoring frequency to daily</p> <p>5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented</p> <p>6. Arrange meeting with IC(E) and ER to discuss the remedial actions to be taken</p> <p>7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER to discuss the remedial action to be taken</p> <p>8. If exceedance stops, cease additional monitoring</p>	<p>1. Check monitoring data submitted by ET</p> <p>2. Check Contractor's working method.</p> <p>3. Discuss with ET and Contractor on possible remedial measures</p> <p>4. Advise the ER on the effectiveness of the proposal remedial measures</p> <p>5. Supervisor implementation of remedial measures</p> <p>1. Discuss amongst ER, ET, and Contractor on potential remedial actions</p> <p>2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly</p> <p>3. Supervise the implementation of remedial measures</p>	<p>1. Confirm receipt of notification of failure in writing</p> <p>2. Notify Contractor</p> <p>3. Ensure remedial measures properly implemented</p> <p>1. Confirm receipt of notification of failure in writing</p> <p>2. Notify Contractor</p> <p>3. In consultation with the IC(E), agreed measures to be implemented</p> <p>4. Ensure remedial measures properly implemented</p> <p>5. If exceedance continues, consider what portion of this work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.</p>	<p>1. Take immediate action to avoid further exceedance</p> <p>2. Submit proposal for remedial actions to IC(E) within 3 working days of notification</p> <p>3. Implement the agreed proposals</p> <p>4. Amend proposal if appropriate</p> <p>1. Take immediate action to avoid further exceedance</p> <p>2. Submit proposals for remedial actions to IC(E) within 3 working days of notification</p> <p>3. Implement the agreed proposals</p> <p>4. Resubmit proposals if possible still not under control</p> <p>5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.</p>	

Event / Action Plan for Construction Noise

EVENT	ET Leader	ACTION			CNTRACTOR
		IC(E)	ER		
Action Level	<ol style="list-style-type: none"> 1. Notify IC(E) and Contractor 2. Carry out investigation 3. Report the results of investigation to the IC(E) and Contractor 4. Discuss with the Contractor and formulate remedial measures 5. Increase monitoring frequency to check mitigation effectiveness 	<ol style="list-style-type: none"> 1. Review the analyzed results submitted by the ET 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly 3. Supervise the implementation of remedial measures 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing 2. Notify Contractor 3. Require Contractor to propose remedial measures for the analyzed noise problem 4. Ensure remedial measures are properly implemented 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposal to IC(E) 2. Implement noise mitigation proposals 	
Limit Level	<ol style="list-style-type: none"> 1. Notify IC(E), ER, and Contractor 2. Identify source 3. Repeat measurement to confirm findings 4. Increase monitoring frequency 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented 6. Inform IC(E), ER and EPD the causes & action taken for the exceedances 7. Assess effectiveness of Contractor's remedial action and keep IC(E), EPD and ER informed to the results 8. If exceedance stops, cease additional monitoring 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET and Contractor on the potential remedial actions 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly 3. Supervise the implementation of remedial measures 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing 2. Notify Contractor 3. Require Contractor to propose remedial measures for the analysed noise problem 4. Ensure remedial measures are properly implemented 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification 3. Implement the agreed proposals 4. Resubmit proposals if problem still not under control 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated 	



Appendix F

Construction Programme



Act ID	Description	Total Float	Percent Complete	Entry Start	Entry Finish	Late Start	Late Finish
CD0100	Section 1	0	0	15MAR07	15MAR07		
CD0200	Section 2	0	0	28JUL07	28JUL07		
CD0300	Section 3	0	0	23JUN07	23JUN07		
CD0400	Section 4	0	0	29MAY07	29MAY07		
CD0700	Section 7	0	0	03APR07	03APR07		
CD0800	Section 8	0	0	17MAY07	17MAY07		
CD0900	Section 9	0	0	16FEB07	16FEB07		
CD1100	Section 11	0	0	26MAR07	26MAR07		
CD1200	Section 12	0	0	23APR07	23APR07		
CD1300	Section 13	0	0	09MAY07	09MAY07		
CD1400	Section 14	0	0	28MAR08	28MAR08		
CD1500	Section 15	0	0	23APR08	23APR08		
CD1600	Section 16	0	0	09MAY08	09MAY08		
Teststone							
Section 5							
MSS50100	Complete Laying of Utilities	0	0	19JAN07	19JAN07		31JUL06*
Section 7							
MSS70100	Complete Connection for ArchSD's Works	0	0	19JAN07	19JAN07		31JUL06*
MSS70300	Complete Toilet & Pavilion by ASD's Contractor	0	0	23JAN07	23JAN07		05NOV05*
Section 8							
MSS80100	Complete Connection of Utilities	0	0	19JAN07	19JAN07		20APR06*
MSS80200	Commence ASD's Works	0	0	20JAN07	20JAN07		29MAR06
MSS80300	Complete ASD's Works	0	0	17MAY07	17MAY07		22JUL06*
Section 1							
Amenity Area							
A1AMDW100	CCTV Inspection	10	0	30JAN07	09FEB07	05MAR07	15MAR07
Drainage Works							
A1AMUT0100	Planter Watermain - M9 to WP9-4 (South Section)	15	0	20JAN07	08FEB07	01FEB07	21FEB07
A1AMUT0200	Planter Watermain - M7 to WP7-4 (North Section)	15	0	25JAN07	10FEB07	01FEB07	21FEB07
A1AMUT0300	Install Public Lighting Post (by Hyd)	10	0	20JAN07	31JAN07	05MAR07	15MAR07
Public Lighting, Duct and Trub							
A1AMPK0200	Construct Dwarf Wall (North Section)	21	80	10NOV06 A	24JAN07	10NOV06 A	24JAN07
A1AMPK0300	Construct Edging Beam (South Section)	22	50	21NOV06 A	01FEB07	21NOV06 A	03MAR07
A1AMPK0400	Construct Edging Beam (North Section)	18	50	16OCT06 A	30JAN07	16OCT06 A	03MAR07
A1AMPK0500	Lighting Drawpit & Cable Duct (South Section)	14	30	08JAN07 A	13FEB07	08JAN07 A	15MAR07
A1AMPK0600	Lighting Drawpit & Cable Duct (North Section)	14	30	15JAN07 A	10FEB07	15JAN07 A	15MAR07
Roads and Pavmg							

Act ID: 10JUN04
 Description: Progress bar
 Start date: 09MAY08
 Finish date: 20JAN07
 Act ID: 08FEB07
 Description: Critical bar
 Start date: 08FEB07
 Finish date: 08FEB07
 Act ID: 1A
 Description: Summary bar
 Start date: 08FEB07
 Finish date: 08FEB07

10JUN04
 09MAY08
 20JAN07
 08FEB07
 08FEB07

Start milestone point

Leader - Wai Kee (C&T) Joint Venture
TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)

Act ID	Description	Original Duration	Percent Complete	Total Float	Early Start	Early Finish	Late Start	Late Finish	
A2MBR0200	Erect Signage	12	0	24d	08JUN07	22JUN07	09JUL07	21JUL07	
Retaining Wall									
No. 1									
A2REWA1210	Upstand Wall for Retaining Wall No. 1	35	20	16d	10DEC06 A	24FEB07	10DEC06 A	15MAR07	
Road D1									
Drainage Works									
A2RDDW0200	S615 - Existing Manhole	36	5	53d	21DEC06 A	10MAR07	21DEC06 A	14MAY07	
A2RDDW0210	F304 - F308 (VO128)	42	0	53d	20JAN07	13MAR07	27MAR07	16MAY07	
A2RDDW0300	S628 - S628	31	0	46d	27MAR07	03MAY07	15MAY07	20JUN07	
A2RDDW0350	S616 - S629	24	0	92d	20JAN07	16FEB07	14MAY07	09JUN07	
A2RDDW0410	Alignment confirmation and UU diversion (VO169)	40	0	0	20JAN07	10MAR07	20JAN07	10MAR07	
A2RDDW0500	F310-Existing MH, S610A - S610 (TTA No. 74, 75)	20	0	0	12MAR07	03APR07	12MAR07	03APR07	
A2RDDW0600	F309-F310, S610 - S608 (TTA No. 89)	20	0	0	04APR07	27APR07	04APR07	27APR07	
A2RDDW0700	Replace 600 Pipe by 900 Pipe (TTA No. 91)	20	0	4d	31MAY07	23JUN07	05JUN07	28JUN07	
A2RDDW0800	Reconstruct Ext MH w 1800 Chamber (TTA No. 91)	22	0	4d	31MAY07	25JUN07	05JUN07	30JUN07	
A2RDDW0900	Construct Gullies to Existing Pipe (TTA No. 91)	18	0	0	08JUN07	30JUN07	09JUN07	30JUN07	
Utility Works									
A2RDUT0300	NWT & HGC - Laying Cable Duct	21	0	26d	20JAN07	15FEB07	23FEB07	19MAR07	
A2RDUT0310	NWT & HGC Cable Connection	14	0	53d	14FEB07	06MAR07	21APR07	08MAY07	
A2RDUT0400	WT&T - Laying Cable Duct	21	0	26d	12FEB07	10MAR07	17MAR07	11APR07	
A2RDUT0410	WT&T - Cable Connection	14	0	32d	14MAR07	29MAR07	21APR07	08MAY07	
A2RDUT0500	PCCW - Laying Cable Duct	21	0	32d	12FEB07	10MAR07	24MAR07	18APR07	
A2RDUT0510	PCCW - Cable Connection	14	0	35d	14MAR07	29MAR07	25APR07	11MAY07	
A2RDUT0600	Watermain - Laying FW Main Crossing	12	0	101d	27JAN07	08FEB07	31MAY07	13JUN07	
A2RDUT0700	Watermain - FW Main T to Existing (TTA No. 91)	8	0	0	31MAY07	08JUN07	31MAY07	08JUN07	
A2RDUT1000	Install Public Lighting Post (TTA No. 89)	8	0	56d	14MAY07	22MAY07	20JUL07	28JUL07	
A2RDUT1100	Install Public Lighting Post (TTA No. 91)	8	0	8d	07JUL07	16JUL07	16JUL07	26JUL07	
Public Lighting, Duct and Kerb									
A2RDPK0100	Lay Kerb	14	0	72d	02APR07	18APR07	28JUN07	14JUL07	
A2RDPK0200	Lay Kerb (TTA No. 89)	6	0	0	07MAY07	12MAY07	07MAY07	12MAY07	
A2RDPK0300	Lay Kerb (TTA No. 91)	6	0	0	29JUN07	06JUL07	29JUN07	06JUL07	
A2RDPK0400	Construct Central Divider	24	0	76d	12MAR07	09APR07	11JUN07	10JUL07	
A2RDPK0500	Construct Central Divider (TTA No. 91)	12	0	22d	28MAY07	08JUN07	23JUN07	07JUL07	
A2RDPK0600	Construct CPB	24	0	76d	12MAR07	09APR07	11JUN07	10JUL07	
A2RDPK0700	Lighting Drawpit & Cable Duct	18	0	62d	12MAR07	31MAR07	25MAY07	14JUN07	
A2RDPK0800	Lighting Drawpit & Cable Duct (TTA No. 89)	6	0	0	28APR07	05MAY07	29APR07	05MAY07	
A2RDPK0900	Lighting Drawpit & Cable Duct (TTA No. 91)	6	0	0	29JUN07	06JUL07	29JUN07	06JUL07	
Roads and Pavings									
A2RDRP0100	Trim Formation & Lay Subbase	20	0	72d	02APR07	25APR07	28JUN07	21JUL07	
A2RDRP0200	Trim Formation & Lay Subbase (TTA No. 74, 75)	10	0	68d	14APR07	25APR07	06JUL07	17JUL07	
A2RDRP0300	Trim Formation & Lay Subbase (TTA No. 74, 75)	6	0	68d	04APR07	11APR07	26JUN07	03JUL07	
A2RDRP0400	Trim Formation & Lay Subbase (TTA No. 89)	6	0	0	09MAY07	15MAY07	09MAY07	15MAY07	




Act ID	Description	Original Duration	Percent Complete	Total Float	Early Start	Early Finish	Late Start	Late Finish	2008													
									DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	
A2RRM0500	Fabricate and Install Sign Gantry across S13	48	0	21d	08MAY07	04JUL07	01JUN07	28JUL07														
Existing Sai Cheung Street																						
Drainage Works																						
A2SCDW0200	S654 - S647 (TTA No. 89)	42	0	48d	08FEB07	29MAR07	09APR07	28MAY07														
A2SCDW0300	Construct Gullies (TTA No. 91)	4	0	22d	31MAY07	04JUN07	27JUN07	30JUN07														
Utility Works																						
A2SCUT0900	Install Public Lighting Post (TTA No. 89)	8	0	86d	02MAY07	10MAY07	20JUL07	28JUL07														
A2SCUT1000	Install Public Lighting Post (TTA No. 91)	8	0	22d	20JUN07	28JUN07	17JUL07	25JUL07														
Public Lighting, Duct and Kerb																						
A2SCPK0100	Lay Kerb (TTA No. 89)	8	0	48d	21APR07	30APR07	20JUN07	28JUN07														
A2SCPK0200	Lay Kerb (TTA No. 91)	6	0	22d	12JUN07	18JUN07	10JUL07	16JUL07														
A2SCPK0300	Lighting Drawpit & Cable Duct (TTA No. 89)	8	0	48d	14APR07	23APR07	12JUN07	21JUN07														
A2SCPK0400	Lighting Drawpit & Cable Duct (TTA No. 91)	6	0	22d	06JUN07	11JUN07	03JUL07	08JUL07														
Roads and Paving																						
A2SCRP0100	Trim Formation & Lay Subbase (TTA No. 89)	12	0	48d	21APR07	05MAY07	20JUN07	04JUL07														
A2SCRP0200	Road Pavement (TTA No. 89)	12	0	48d	28APR07	12MAY07	27JUN07	11JUL07														
A2SCRP0300	Road Pavement (TTA No. 91)	8	0	22d	20JUN07	28JUN07	17JUL07	25JUL07														
A2SCRP0400	Remove Existing Traffic Island (TTA No. 90)	28	0	100d	20JAN07	24FEB07	23MAY07	25JUN07														
A2SCRP0500	Road Pavement (TTA No. 90)	28	0	100d	28FEB07	29MAR07	28JUN07	28JUL07														
Road Marking - Traffic Sign and Fencing																						
A2SCRM0050	Apply Road Marking (TTA No. 89)	1	0	68d	14MAY07	14MAY07	28JUL07	28JUL07														
A2SCRM0100	Apply Road Marking (TTA No. 91)	3	0	22d	28JUN07	03JUL07	28JUL07	28JUL07														
A2SCRM0200	Erect Signage	12	0	48d	14MAY07	28MAY07	12JUL07	25JUL07														
A2SCRM0300	Install Railing, Fencing & etc	12	0	48d	14MAY07	28MAY07	12JUL07	25JUL07														
Existing Sai Cheung Street Roundabout																						
Public Lighting, Duct and Kerb																						
A2SRPK0100	Laying Lighting Cross Road Duct (TTA No. 90)	21	0	103d	02FEB07	01MAR07	08JUN07	04JUL07														
A2SRPK0200	Laying Lighting Cross Road Duct (TTA No. 90)	21	0	96d	02FEB07	01MAR07	31MAY07	25JUN07														
Roads and Paving																						
A2SRRP0100	Demolish Existing Island (TTA No. 90)	21	50	103d	20DEC06 A	01FEB07	20DEC06 A	07JUN07														
A2SRRP0200	Construct Proposed Island (TTA No. 90)	21	0	103d	02MAR07	26MAR07	05JUL07	28JUL07														
A2SRRP0300	Demolish Existing Kerb (TTA No. 90)	21	50	96d	03JAN07 A	01FEB07	03JAN07 A	30MAY07														
A2SRRP0400	Lay Kerb (TTA No. 90)	21	0	96d	02MAR07	26MAR07	26JUN07	20JUL07														
A2SRRP0500	Demolish Existing Roundabout (TTA No. 91)	14	0	3d	31MAY07	15JUN07	04JUN07	20JUN07														
A2SRRP0600	Reconstruct Roundabout (TTA No. 91)	10	0	3d	16JUN07	28JUN07	21JUN07	03JUL07														
A2SRRP0700	Reinstate Road Pavement (TTA No. 90)	7	0	96d	27MAR07	05APR07	21JUL07	28JUL07														
A2SRRP0800	Resurfacing Wearing Course	8	0	3d	28JUN07	08JUL07	04JUL07	12JUL07														
A2SRRP0900	Construct Proposed Island (TTA No. 91)	21	0	6d	31MAY07	25JUN07	07JUN07	03JUL07														
Road Marking - Traffic Sign and Fencing																						
A2SRRM0100	Apply Road Marking	2	0	3d	24JUL07	25JUL07	27JUL07	28JUL07														
A2SRRM0200	Erect Signage	12	0	3d	10JUL07	23JUL07	13JUL07	26JUL07														
A2SRRM0300	Install Railing, Fencing & etc	12	0	3d	10JUL07	23JUL07	13JUL07	26JUL07														
Existing Ma Liu Shui Bridge																						
Apply Road Marking																						
Erect Signage																						
Install Railing, Fencing & etc																						
Apply Road Marking																						
Erect Signage																						
Install Railing, Fencing & etc																						

Act ID	Description	Original Duration	Percent Complete	Total Float	Early Start	Early Finish	Late Start	Late Finish
Utility Works								
A2EBR0100	Install Public Lighting Post	8	0	28d	14JUN07	23JUN07	18JUL07	27JUL07
Public Lighting, Duct and Kerb								
A2EBR0100	Lay Kerb (TTA No. 81-85)	21	0	28d	28FEB07	23MAR07	02APR07	26APR07
A2EBR0200	Cable Duct Laying on Island (TTA No. 81-85)	21	0	35d	27APR07	23MAY07	08JUN07	04JUL07
A2EBR0300	Cable Duct Laying on Reserve (TTA No. 81-85)	12	0	26d	12MAY07	25MAY07	14JUN07	28JUN07
Roads and Paving								
A2EBR0100	Demolish Existing Parapet (TTA No. 81-85)	14	0	23d	20APR07	07MAY07	18MAY07	02JUN07
A2EBR0200	Demolish Island & Paved Area (TTA No. 81-85)	14	10	26d	08JAN07 A	27FEB07	08JAN07 A	31MAR07
A2EBR0300	Road Pavement (TTA No. 81-85)	14	0	26d	24MAR07	10APR07	27APR07	14MAY07
A2EBR0400	Construct R/A on V-Abutment (TTA No. 81-85)	21	0	23d	08MAY07	31MAY07	04JUN07	28JUN07
A2EBR0500	Remove Pavement at Proposed Island (TTA No. 81-85)	14	0	28d	11APR07	29APR07	15MAY07	30MAY07
A2EBR0600	Construct Traffic Island (TTA No. 81-85)	8	0	35d	23MAY07	31MAY07	05JUL07	13JUL07
A2EBR0700	Construct Remaining Roundabout (TTA No. 81-85)	12	0	23d	01JUN07	14JUN07	28JUN07	13JUL07
A2EBR0800	Demolish Existing Cent. Reserve (TTA No. 81-85)	12	0	26d	27APR07	11MAY07	31MAY07	13JUN07
A2EBR0900	Rectification of existing MJ & waterproofing	60	0	39d	28FEB07	10MAY07	16APR07	28JUN07
A2EBR0900	Construct New Cent. Reserve (TTA No. 81-85)	18	0	26d	24MAY07	13JUN07	27JUN07	18JUL07
Road Marking, Traffic Sign and Fencing								
A2EBR0100	Apply Road Marking (TTA No. 92-93, 88)	1	0	35d	15JUN07	15JUN07	28JUL07	28JUL07
A2EBR0200	Apply Road Marking (TTA No. 92-93, 88)	1	0	26d	30JUN07	30JUN07	28JUL07	28JUL07
A2EBR0300	Erect Signage	12	0	26d	15JUN07	28JUN07	14JUL07	27JUL07
A2EBR0400	Install Railing, Fencing & etc	12	0	23d	15JUN07	28JUN07	14JUL07	27JUL07
Car Park and Access Road								
Utility Works								
A2CPT0500	Install Public Lighting Post	8	0	70d	26APR07	05MAY07	20JUL07	28JUL07
Public Lighting, Duct and Kerb								
A2CPR0100	Construct Dwarf Wall	23	0	22d	02MAR07	28MAR07	28MAR07	24APR07
A2CPR0200	Lay Kerb	8	0	52d	17APR07	25APR07	18JUN07	27JUN07
A2CPR0300	Public Lighting Controller	10	0	83d	25MAR07	10APR07	08JUL07	18JUL07
A2CPR0400	Lighting Drawpit & Cable Duct	15	0	52d	29MAR07	16APR07	31MAY07	16JUN07
Roads and Paving								
A2CPR0100	Trim Formation & Lay Subbase	8	0	60d	26APR07	05MAY07	08JUL07	17JUL07
A2CPR0200	Road Pavement	8	0	60d	07MAY07	15MAY07	16JUL07	26JUL07
A2CPR0300	Construct Footpath	18	0	52d	26APR07	17MAY07	28JUN07	19JUL07
Road Marking, Traffic Sign and Fencing								
A2CPR0100	Apply Road Marking	2	0	52d	25MAY07	26MAY07	27JUL07	28JUL07
A2CPR0200	Erect Signage	6	0	52d	18MAY07	24MAY07	20JUL07	26JUL07
A2CPR0300	Install Railing, Fencing & etc	6	0	52d	18MAY07	24MAY07	20JUL07	26JUL07
Amenity Area								
Drainage Works								
A2AMD0100	Construct U-Channels	18	0	83d	29MAR07	19APR07	09JUL07	28JUL07
Utility Works								
A2AMU0100	Water Point WPI-3 to Water Meter No.1	18	0	62d	10APR07	30APR07	23JUN07	14JUL07

Start date: 10JUN04
 Finish date: 09MAY08
 Start date: 20JUN07
 Finish date: 06FEB07
 Page number: 7A

Legend:
 Early bar
 Progress bar
 Critical bar
 Summary bar
 Start milestone point



Leader - Wai Kee (C&T) Joint Venture
TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)

Act ID	Description	Total Float	Percent Complete	Early Start	Early Finish	Late Start	Late Finish
A2AMUT0200	Water Point WP2-3 to Water Meter No.2	83d	0	30MAR07	19APR07	10JUL07	28JUL07
A2AMUT0300	Water Point WP3-5 to Water Meter No.3	82d	0	14APR07	15MAY07	28JUN07	28JUL07
A2AMUT0400	Water Point WP2-2 to Water Meter No.8	82d	0	02MAY07	15MAY07	18JUL07	28JUL07
Section 3							
Ma Liu Shui Subway							
Pump House Construction							
A3MSPH0300	Construct Wall up to Top Slab	50	0	06DEC06 A	26JAN07	09DEC06 A	07FEB07
A3MSPH0400	Construct Top Slab	0	0	27JAN07	09FEB07	09FEB07	24FEB07
A3MSPH0500	Install Hoisting Beam	0	0	03FEB07	09FEB07	15FEB07	24FEB07
Subway Barrel Construction							
A3MSSB0900	Construct Subway #4 Wall + Top Slab	80	0	25DEC06 A	09FEB07	25DEC06 A	24FEB07
A3MSSB1000	Backfilling	0	0	03FEB07	27FEB07	15FEB07	10MAR07
Subway East Ramp Construction							
A3MSSZ2700	Install Roof Steel Posts	0	0	16FEB07	02MAR07	03MAR07	14MAR07
A3MSSZ2800	Construct Roof Slab E6	0	0	03MAR07	16MAR07	15MAR07	28MAR07
A3MSSZ2900	Construct Roof Slab E5	0	0	17MAR07	30MAR07	29MAR07	12APR07
A3MSSZ3000	Construct Roof Slab E4, E7	0	0	31MAR07	14APR07	13APR07	26APR07
A3MSSZ3100	Construct Roof Slab E3, E8	0	0	03MAR07	16MAR07	15MAR07	28MAR07
A3MSSZ3200	Construct Roof Slab E2	0	0	17MAR07	30MAR07	29MAR07	12APR07
A3MSSZ3300	Construct Roof Slab E1, E9	0	0	31MAR07	14APR07	13APR07	26APR07
Subway West Ramp Construction							
A3MSSW1400	Construct W5 Ramp Walls	7	0	25JAN07	01FEB07	09FEB07	16FEB07
A3MSSW1500	Construct W6 Ramp Walls	60	0	14JAN07 A	24JAN07	14JAN07 A	08FEB07
A3MSSW1600	Backfilling	20	0	02FEB07	28FEB07	21FEB07	15MAR07
A3MSSW1700	Install Roof Posts	18	0	15FEB07	10MAR07	06MAR07	28MAR07
A3MSSW1800	Construct Roof Slab W3	12	0	12MAR07	24MAR07	27MAR07	10APR07
A3MSSW1900	Construct Roof Slab W4	12	0	26MAR07	09APR07	11APR07	24APR07
A3MSSW2000	Construct Roof Slab W2, W5	12	0	26MAR07	09APR07	11APR07	24APR07
A3MSSW2100	Construct Roof Slab W1, W6	12	0	12MAR07	24MAR07	11APR07	24APR07
Pumping and Drainage System							
A3MSPD0100	Pumping System Installation	30	0	10FEB07	20MAR07	22MAR07	26APR07
A3MSPD0200	Drainage System Installation (Barrel)	7	0	28FEB07	07MAR07	29MAR07	06APR07
A3MSPD0210	Drainage System Installation (East Ramp)	7	0	16APR07	23APR07	27APR07	05MAY07
A3MSPD0220	Drainage System Installation (West Ramp)	7	0	10APR07	17APR07	25APR07	03MAY07
Miscellaneous works							
A3MSMW0100	Miscellaneous Metal Works	24	0	11MAY07	07JUN07	26MAY07	23JUN07
Finishing Works							
A3MSFW0100	Finishing Works at Barrel	24	0	06MAR07	04APR07	07APR07	05MAY07
A3MSFW0200	Finishing Works at East Ramp	24	0	10APR07	22MAY07	07MAY07	02JUN07
A3MSFW0300	Finishing Works at West Ramp	24	0	18APR07	19MAY07	04MAY07	31MAY07
E. & M Works							
A3MSEM0100	Electrical Installation at Barrel & Pump House	24	0	28MAR07	26APR07	27APR07	25MAY07
A3MSEM0200	Electrical Installation at East Ramp	24	0	15MAY07	11JUN07	26MAY07	23JUN07

Construct Wall up to Top Slab
 Construct Top Slab
 Install Hoisting Beam
 Construct Subway #4 Wall + Top Slab
 Backfilling
 Install Roof Steel Posts
 Construct Roof Slab E6
 Construct Roof Slab E5
 Construct Roof Slab E4, E7
 Construct Roof Slab E3, E8
 Construct Roof Slab E2
 Construct Roof Slab E1, E9
 Construct W5 Ramp Walls
 Construct W6 Ramp Walls
 Backfilling
 Install Roof Posts
 Construct Roof Slab W3
 Construct Roof Slab W4
 Construct Roof Slab W2, W5
 Construct Roof Slab W1, W6
 Pumping System Installation
 Drainage System Installation (Barrel)
 Drainage System Installation (East Ramp)
 Drainage System Installation (West Ramp)
 Miscellaneous Metal Works -
 Finishing Works at Barrel
 Finishing Works at East Ramp
 Finishing Works at West Ramp
 Electrical Installation at Barrel & Pump House
 Electrical Installation at East Ramp

Start date 10JUN04
 Finish date 09MAY08
 Data date 20JAN07
 Run date 06FEB07
 Page number 8A

Early bar
 Progress bar
 Critical bar
 Summary bar
 Start milestone point


Leader - Wai Kee (C&T) Joint Venture
 TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)

Act ID	Description	Original Duration	Percent Complete	Total Float	Early Start	Early Finish	Late Start	Late Finish
A3MBEM300	Electrical Installation at West Ramp	24	0	15d	09MAY07	05JUN07	28MAY07	23JUN07
A3MSTC0100	Pumping System & Electrical Installation	24	0	25d	26APR07	24MAY07	28MAY07	23JUN07
Drainage Works								
A3LUDW0700	S687 - S622	21	0	14d	01MAR07	24MAR07	17MAR07	11APR07
A3LUDW0800	S617 - S618	11	0	24d	01MAR07	13MAR07	29MAR07	11APR07
A3LUDW1000	S614 - S623 (TTA no. 91)	20	0	14d	02MAR07	24MAR07	19MAR07	11APR07
A3LUDW1100	S693 - S634	21	60	13d	10JUL06 A	28JAN07	10JUL06 A	19FEB07
Utility Works								
A3LUUT0100	CLP - Laying LV Cable	5	0	13d	26MAR07	30MAR07	11APR07	16APR07
A3LUUT0200	CLP - Construct Pillar Box	5	0	29d	01MAR07	06MAR07	04APR07	10APR07
A3LUUT0300	Install Public Lighting Post	8	0	0	14JUN07	23JUN07	14JUN07	23JUN07
Public Lighting, Duct and Kerb								
A3LUPK0100	Construct Dwarf Wall	35	0	13d	16FEB07	31MAR07	07MAR07	17APR07
A3LUPK0200	Construct Dwarf Wall (TTA No. 89)	6	0	14d	28MAR07	31MAR07	12APR07	18APR07
A3LUPK0300	Lay Kerb (TTA No. 89)	12	0	13d	23APR07	07MAY07	09MAY07	22MAY07
A3LUPK0400	Lay Kerb (TTA No. 91)	6	0	0	31MAY07	06JUN07	31MAY07	06JUN07
A3LUPK0500	Lighting Drawpit & Cable Duct (TTA No. 89)	18	0	13d	31MAR07	21APR07	17APR07	08MAY07
A3LUPK0600	Lighting Drawpit & Cable Duct (TTA No. 91)	6	0	0	07JUN07	13JUN07	07JUN07	13JUN07
Roads and Pavings								
A3LURP0100	Trim Formation & Lay Subbase (TTA No. 91)	8	0	0	02JUN07	11JUN07	02JUN07	11JUN07
A3LURP0200	Road Pavement (TTA No. 91)	8	0	0	12JUN07	21JUN07	12JUN07	21JUN07
A3LURP0300	Construct Footpath (TTA No. 89)	24	0	13d	08MAY07	04JUN07	23MAY07	20JUN07
A3LURP0400	Construct Footpath (TTA No. 91)	6	0	5d	07JUN07	13JUN07	13JUN07	20JUN07
Road Marking, Traffic Sign and Fencing								
A3LURM0100	Apply Road Marking	2	0	0	23JUN07	23JUN07	23JUN07	23JUN07
A3LURM0200	Erect Signage	6	0	5d	08JUN07	15JUN07	15JUN07	22JUN07
A3LURM0300	Install Railing, Fencing & etc	6	0	5d	08JUN07	15JUN07	15JUN07	22JUN07
Amenity Area								
A3AMDV0100	Construct U-Channels	36	0	33d	02APR07	16MAY07	12MAY07	23JUN07
Utility Works								
A3AMUT0100	Water Point WPA-2 to Water Meter No.3	16	0	23d	10APR07	27APR07	08MAY07	25MAY07
A3AMUT0200	Water Point WPS-2 to Water Meter No.5	10	0	23d	28APR07	10MAY07	28MAY07	06JUN07
A3AMUT0300	Water Point WPS-2 to Water Meter No.6	14	0	23d	11MAY07	28MAY07	07JUN07	23JUN07
Section 4								
Public Toilet No. 2								
Ground Floor Slab Construction								
A4PTGF0100	Erect Propping & Formwork	14	0	0	20JAN07	05FEB07	20JAN07	05FEB07
A4PTGF0200	Ground Slab Steel Fixing	3	0	0	06FEB07	08FEB07	06FEB07	08FEB07
A4PTGF0300	Formwork	2	0	0	09FEB07	10FEB07	09FEB07	10FEB07
A4PTGF0400	Concreting	1	0	0	12FEB07	12FEB07	12FEB07	12FEB07
A4PTGF0500	Erect Scaffolding	3	0	0	13FEB07	15FEB07	13FEB07	15FEB07

Start date: 10JUN04
 Finish date: 09MAY08
 Start date: 20JAN07
 Start date: 06FEB07
 Sign number: 9A

Legend:
 ■ Early bar
 ■ Progress bar
 ■ Critical bar
 ■ Summary bar
 ◆ Start milestone point

Leader - Wai Kee (C&T) Joint Venture
TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)



Act ID	Description	Original Duration	Percent Complete	Total Float	Early Start	Early Finish	Late Start	Late Finish	2006												
					DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC				
A4PTGF0600	Walls & Columns Formwork	3	0	0	16FEB07	22FEB07	16FEB07	22FEB07													
A4PTGF0700	Steel Fixing for Walls & Columns	3	0	0	23FEB07	28FEB07	23FEB07	28FEB07													
A4PTGF0800	Formwork	3	0	0	27FEB07	01MAR07	27FEB07	01MAR07													
A4PTGF0900	Concreting	1	0	0	02MAR07	02MAR07	02MAR07	02MAR07													
A4PTGF1000	Remove Formwork & Propping	12	0	10d	03MAR07	18MAR07	15MAR07	28MAR07													
Mezzanine Floor Slab Construction																					
A4PTMF0100	Erect Propping & Formwork	6	0	0	03MAR07	03MAR07	03MAR07	09MAR07													
A4PTMF0200	Mezzanine Slab Steel Fixing	3	0	0	10MAR07	13MAR07	10MAR07	13MAR07													
A4PTMF0300	Formwork	2	0	0	14MAR07	15MAR07	14MAR07	15MAR07													
A4PTMF0400	Concreting	1	0	0	16MAR07	16MAR07	16MAR07	16MAR07													
A4PTMF0500	Walls & Columns Formwork	3	0	0	17MAR07	20MAR07	17MAR07	20MAR07													
A4PTMF0600	Steel Fixing for Walls & Columns	3	0	0	21MAR07	23MAR07	21MAR07	23MAR07													
A4PTMF0700	Formwork	3	0	0	24MAR07	27MAR07	24MAR07	27MAR07													
A4PTMF0800	Concreting	1	0	0	28MAR07	28MAR07	28MAR07	28MAR07													
A4PTMF0900	Remove Formwork & Propping	12	0	0	29MAR07	12APR07	29MAR07	12APR07													
Upper Mezzanine Floor Slab Construction																					
A4PTUF0100	Erect Propping & Formwork	6	0	0	29MAR07	04APR07	29MAR07	04APR07													
A4PTUF0200	Upper Mezzanine Slab Steel Fixing	3	0	0	06APR07	09APR07	06APR07	09APR07													
A4PTUF0300	Formwork	2	0	0	10APR07	11APR07	10APR07	11APR07													
A4PTUF0400	Concreting	1	0	0	12APR07	12APR07	12APR07	12APR07													
A4PTUF0500	Remove Formwork & Propping	12	0	0	13APR07	26APR07	13APR07	26APR07													
Structural Steelworks																					
A4PTSS0400	Delivery of Structural Steel Materials	12	30	0	16JAN07 A	26JAN07	16JAN07 A	26JAN07													
A4PTSS0500	Inspection & Testing	18	0	0	30JAN07	22FEB07	30JAN07	22FEB07													
A4PTSS0600	Fabrication & Painting of Steelworks	42	0	0	23FEB07	13APR07	23FEB07	13APR07													
A4PTSS0700	Delivery of Prefabricated Steelworks	12	0	0	14APR07	27APR07	14APR07	27APR07													
A4PTSS0800	Erection of Steelworks	21	0	0	29APR07	23MAY07	29APR07	23MAY07													
A4PTSS0900	Touch Up Painting	12	0	0	16MAY07	29MAY07	16MAY07	29MAY07													
Architectural Builders Works and Finishes																					
A4PTAB0100	Solid Concrete Block Work Wall	21	0	0	29MAR07	23APR07	29MAR07	23APR07													
A4PTAB0200	Internal Wall Tile	21	0	0	16APR07	10MAY07	16APR07	10MAY07													
A4PTAB0300	External Wall Tile	21	0	0	27APR07	22MAY07	27APR07	22MAY07													
A4PTAB0400	Toilet Accessories Installation	21	0	15d	17APR07	11MAY07	05MAY07	29MAY07													
A4PTAB0500	Floor Tile	21	0	0	05MAY07	29MAY07	05MAY07	29MAY07													
A4PTAB0600	Roof Cladding	21	0	0	05MAY07	29MAY07	05MAY07	29MAY07													
A4PTAB0700	Metal Works & Ironmongery Installation	21	0	0	05MAY07	29MAY07	05MAY07	29MAY07													
Plumbing Works																					
A4PTPL0100	Plumbing Works (Internal Structure)	21	0	0	05MAY07	29MAY07	05MAY07	29MAY07													
E & M Works																					
A4PTEM0100	Electrical & Mechanical Installations	42	0	0	31MAR07	21MAY07	31MAR07	21MAY07													
A4PTEM0110	Testing and Commissioning	7	0	0	22MAY07	29MAY07	22MAY07	29MAY07													



Leader - Wai Kee (C&T) Joint Venture
 TP37/03 - Critical Path Reference Program for RP-10 (Progress Updated to 20 January 2007)

Start date	10JUN04
Finish date	09MAY08
Issue date	20JAN07
Run date	09FEB07
Page number	10A

Early bar
 Progress bar
 Critical bar
 Summary bar
 Start milestone point

Act ID	Description	Total Float	Percent Complete	Original Duration	Early Start	Early Finish	Late Start	Late Finish
Ramp Wall - North								
A4RAR2200	Backfilling	76d	0	6	20JAN07	26JAN07	26APR07	09MAY07
A4RAR2300	Construct Granite Facing Stone	80d	0	12	27JAN07	09FEB07	07MAY07	19MAY07
A4RAR2400	Paving	76d	0	14	27JAN07	12FEB07	04MAY07	19MAY07
A4RAR2500	Erect Type 2 Railing	76d	0	8	13FEB07	24FEB07	21MAY07	29MAY07
A4RAR2600	Construct Staircase	88d	0	12	27JAN07	09FEB07	16MAY07	29MAY07
Ramp Wall - Tolls								
A4RART1000	Erect Formwork for Wall	20d	1	6	18JAN07 A	26JAN07	18JAN07 A	22FEB07
A4RART1100	Concreting	20d	0	1	27JAN07	27JAN07	23FEB07	23FEB07
A4RART1200	Remove Formwork	20d	0	3	28JAN07	31JAN07	24FEB07	27FEB07
A4RART1400	Backfilling	66d	0	12	01FEB07	14FEB07	24APR07	08MAY07
A4RART1500	Construct Granite Facing Stone	68d	0	10	15FEB07	01MAR07	11MAY07	22MAY07
A4RART1600	Paving	66d	0	12	15FEB07	03MAR07	09MAY07	22MAY07
A4RART1700	Erect Type 2 Railing	66d	0	6	05MAR07	10MAR07	23MAY07	29MAY07
Ramp Wall - South								
A4RARS1700	Steel Fixing for Side Walls (S2)	18d	50	6	18JAN07 A	25JAN07	18JAN07 A	14FEB07
A4RARS1800	Erect Formwork for Side Walls (S2)	19d	0	6	24JAN07	30JAN07	15FEB07	24FEB07
A4RARS1900	Concreting (S2)	19d	0	1	31JAN07	31JAN07	26FEB07	26FEB07
A4RARS2000	Remove Formwork (S2)	19d	0	1	01FEB07	01FEB07	27FEB07	27FEB07
A4RARS2200	Backfilling	65d	0	12	02FEB07	16FEB07	24APR07	08MAY07
A4RARS2300	Construct Granite Facing Stone	71d	0	6	16FEB07	26FEB07	16MAY07	22MAY07
A4RARS2400	Paving	65d	0	12	16FEB07	05MAR07	09MAY07	22MAY07
A4RARS2500	Erect Type 2 Railing	65d	0	6	08MAR07	12MAR07	23MAY07	29MAY07
Section 7								
Waterfront Promenade								
Utility Works								
A7WPU0610	PCCW - Lay Cable (Landscape Node P3)	2d	0	12	20JAN07	02FEB07	23JAN07	05FEB07
Public Lighting, Duct and Cable								
A7WPPK0100	Public Lighting (In ZU)	24d	90	60	03APR06 A	26JAN07	03APR06 A	27FEB07
A7WPPK0200	Public Lighting (In ZS)	6d	60	60	03APR06 A	16FEB07	03APR06 A	27FEB07
Roads and Paving								
A7WPRP0050	Paving works at Foot Message Area	21d	50	18	08JAN07 A	30JAN07	08JAN07 A	27FEB07
A7WPRP0100	Lay asphalt & paving block (In ZU & ZL3)	21d	40	50	12DEC06 A	09MAR07	12DEC06 A	03APR07
A7WPRP0200	Lay asphalt & paving block (In ZS & ZR1)	21d	40	50	21OCT06 A	27FEB07	21OCT06 A	27FEB07
A7WPRP0205	TTA approval in TMLG (Section 7 & 8)	0	0	14	02FEB07	21FEB07	02FEB07	21FEB07
A7WPRP0206	RMO notice for crossing TTA (Section 7 & 8)	0	0	7	02FEB07	01MAR07	22FEB07	01MAR07
A7WPRP0210	Additional 2 nos crossing (VO1568) 1st half	0	0	14	02MAR07	17MAR07	02MAR07	17MAR07
A7WPRP0220	Additional 2 nos crossing (VO1568) 2nd half	0	0	14	19MAR07	03APR07	19MAR07	03APR07
A7WPRP0230	Repare verge adjacent to promenade (VO164)	0	0	28	02MAR07	03APR07	02MAR07	03APR07
Finishing Works								
A7WPFV0100	Finishing Works (In ZU) (include pump room)	39d	30	30	09JAN06 A	13FEB07	09JAN06 A	03APR07
A7WPFV0200	Finishing Works (In ZS)	54d	90	55	13APR06 A	28JAN07	13APR06 A	03APR07

E & M Works

act date	10JUN04		Early bar
finish date	09MAY06		Progress bar
act date	20JAN07		Critical bar
act date	06FEB07		Summary bar
page number	11A		Start milestone point

Leader - Wai Kee (C&T) Joint Venture
TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)



Act ID	Description	Original Duration	Percent Complete	Total Float	Early Start	Early Finish	Late Start	Late Finish	2007												
									JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	
ATWPEM0700	E&M Works	30	75	25d	19AUG06 A	08FEB07	19AUG06 A	13MAR07	E&M Works												
Testing and Commissioning																					
ATWPTC0100	Testing & Commissioning for Section 7	14	0	25d	14FEB07	05MAR07	19MAR07	03APR07	Testing & Commissioning for Section 7												
Road Marking, Traffic Sign and Fencing																					
ATWPRM0300	Erect Signage	20	0	22d	10FEB07	08MAR07	12MAR07	03APR07	Erect Signage												
Landscape Hardworks																					
ATWPHL1600	Public Toilet & Pavilion by ASD's Contractor	297	59	366d	28DEC04 A	23JAN07	28DEC04 A	05NOV05	Public Toilet & Pavilion by ASD's Contractor												
ATWPHL1605	Approval of Litter-bin material (Section 7 & 8)	12	0	0	20JAN07	02FEB07	20JAN07	02FEB07	Approval of Litter-bin material (Section 7 & 8)												
ATWPHL1606	Delivery of Litter-bin material (Section 7 & 8)	63	0	0	03FEB07	21APR07	03FEB07	21APR07	Delivery of Litter-bin material (Section 7 & 8)												
ATWPHL1610	Litter-bin Footing excavation (33 nos) (VO179)	6	0	26d	03FEB07	09FEB07	09MAR07	15MAR07	Litter-bin Footing excavation (33 nos) (VO179)												
ATWPHL1620	Litter-bin footing concreting (VO179)	6	0	26d	10FEB07	16FEB07	16MAR07	22MAR07	Litter-bin footing concreting (VO179)												
ATWPHL1630	Litter-bin paving temp reinstatement (VO179)	10	0	26d	21FEB07	03MAR07	23MAR07	03APR07	Litter-bin paving temp reinstatement (VO179)												
Section 8																					
Waterfront Promenades																					
Drainage Works																					
ABWPDW0400	S729 - S730	14	75	5d	09AUG06 A	24JAN07	09AUG06 A	30JAN07	S729 - S730												
ABWPDW0600	225HR & Catchpit/200DI along P.Wall (ZR) N2-N3	48	20	23d	15AUG06 A	08MAR07	15AUG06 A	04APR07	225HR & Catchpit/200DI along P.Wall (ZR) N2-N3												
ABWPDW0900	225HR & Catchpit/200DI along P.Wall (ZK) N2-PLS	24	0	18d	13FEB07	15MAR07	09MAR07	06APR07	225HR & Catchpit/200DI along P.Wall (ZK) N2-PLS												
ABWPDW1000	225HR & Catchpit/200DI along P.Wall (ZJ6) PLS	12	0	36d	06FEB07	22FEB07	23MAR07	06APR07	225HR & Catchpit/200DI along P.Wall (ZJ6) PLS												
ABWPDW1100	225HR & Catchpit/200DI along P.Wall (ZJ5) PLSN	6	0	37d	30JAN07	05FEB07	17MAR07	23MAR07	225HR & Catchpit/200DI along P.Wall (ZJ5) PLSN												
ABWPDW1200	225HR & Catchpit/200DI along P.Wall (ZJ) PLSN-N1	50	90	53d	15AUG06 A	25JAN07	15AUG06 A	31MAR07	225HR & Catchpit/200DI along P.Wall (ZJ) PLSN-N1												
ABWPDW1300	225HR & Catchpit/200DI along P.Wall (ZM) N1N-TP	30	5	39d	01JAN07 A	26FEB07	01JAN07 A	13APR07	225HR & Catchpit/200DI along P.Wall (ZM) N1N-TP												
ABWPDW1900	150 Perforated Drain (In ZR)	19	90	0	13OCT06 A	22JAN07	13OCT06 A	22JAN07	150 Perforated Drain (In ZR)												
ABWPDW2000	150 Perforated Drain (In ZK)	18	40	2d	17OCT06 A	01FEB07	17OCT06 A	03FEB07	150 Perforated Drain (In ZK)												
ABWPDW2100	150 Perforated Drain (In ZJ6)	9	60	5d	03JAN07 A	29JAN07	03JAN07 A	03FEB07	150 Perforated Drain (In ZJ6)												
ABWPDW2200	150 Perforated Drain (In ZJ5)	5	80	12d	12DEC06 A	20JAN07	12DEC06 A	03FEB07	150 Perforated Drain (In ZJ5)												
ABWPDW2300	150 Perforated Drain (ZJ - Node P1 South)	24	95	16d	05NOV06 A	20JAN07	05NOV06 A	08FEB07	150 Perforated Drain (ZJ - Node P1 South)												
Utility Works																					
ABWPUT0200	Watermain Connection in existing cycle track	28	0	36d	02MAR07	03APR07	14APR07	17MAY07	Watermain Connection in existing cycle track												
ABWPUT0700	PCCW - Lay Cable (In ZR)	48	92	2d	09AUG06 A	24JAN07	09AUG06 A	28JAN07	PCCW - Lay Cable (In ZR)												
ABWPUT0800	PCCW - Lay Cable (In ZK)	22	0	9d	13FEB07	13MAR07	27FEB07	23MAR07	PCCW - Lay Cable (In ZK)												
ABWPUT0900	PCCW - Lay Cable (In ZJ6)	10	0	2d	01FEB07	12FEB07	03FEB07	14FEB07	PCCW - Lay Cable (In ZJ6)												
ABWPUT1000	PCCW - Lay Cable (In ZJ5)	6	0	2d	25JAN07	31JAN07	27JAN07	02FEB07	PCCW - Lay Cable (In ZJ5)												
ABWPUT1100	PCCW - Lay Cable (In ZJ, ZM, ZL1)	44	95	3d	30SEP06 A	22JAN07	30SEP06 A	25JAN07	PCCW - Lay Cable (In ZJ, ZM, ZL1)												
Public Lighting, Duct and Kerb																					
ABWPPK0300	Public Lighting Ducts & Drawpits Along Promenade	60	40	36d	21OCT06 A	06MAR07	21OCT06 A	18APR07	Public Lighting Ducts & Drawpits Along Promenade												
ABWPPK0400	Install Public Lighting	24	0	36d	03FEB07	06MAR07	21MAR07	18APR07	Install Public Lighting												
Roads and Paving																					
ABWPPR0100	Lay asphalt & paving block (ZR) (N2 - N3)	35	0	23d	09MAR07	19APR07	06APR07	17MAY07	Lay asphalt & paving block (ZR) (N2 - N3)												
ABWPPR0200	Lay asphalt & paving block (ZK) (N2 - PLS)	20	0	9d	13APR07	07MAY07	24APR07	17MAY07	Lay asphalt & paving block (ZK) (N2 - PLS)												
ABWPPR0300	Lay asphalt & paving block (ZJ6) (PLS)	14	0	9d	27MAR07	12APR07	07APR07	23APR07	Lay asphalt & paving block (ZJ6) (PLS)												
ABWPPR0400	Lay asphalt & paving block (ZJ5) (PLS N)	10	0	9d	14MAR07	24MAR07	24MAR07	04APR07	Lay asphalt & paving block (ZJ5) (PLS N)												

Start date: 10JUN04
 Finish date: 09MAY08
 Issue date: 20JAN07
 Run date: 06FEB07
 Page number: 12A

Legend:
 [Green Box] Early bar
 [Red Box] Progress bar
 [Black Box] Critical bar
 [Grey Box] Summary bar
 [Diamond] Start milestone point

Leader - Wai Kee (C&T) Joint Venture
TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)

Act ID	Description	Original Duration	Percent Complete	Total Float	Early Start	Early Finish	Late Start	Late Finish	2008																									
									DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC													
ABWPRP0500	Lay asphalt & paving block (ZJ) (PLSN - N1)	40	0	2d	13FEB07	03APR07	15FEB07	06APR07																										
ABWPRP0502	Lay asphalt & paving block (ZM) (M1N - TP)	28	0	38d	27FEB07	30MAR07	14APR07	17MAY07																										
ABWPRP0510	Additional 3 EVA & 2 crossings (VO158B) 1st half	18	0	0	04APR07	25APR07	04APR07	25APR07																										
ABWPRP0520	Additional 3 EVA & 2 crossings (VO158B) 2nd half	18	0	0	26APR07	17MAY07	26APR07	17MAY07																										
ABWPRP0530	Repave verge adjacent to promenade (VO165)	38	0	0	04APR07	17MAY07	04APR07	17MAY07																										
Finishing Works																																		
ABWPFW0100	Finishing Works	60	23	50d	08SEP06	17MAR07	08SEP06	17MAY07																										
E & M Works																																		
ABWPEM0500	Irrigation System	50	20	27d	15JAN07	14APR07	15JAN07	17MAY07																										
ABWPEM1000	E & M Works	30	20	36d	15JAN07	03APR07	15JAN07	17MAY07																										
Road Marking, Traffic Sign and Fencing																																		
ABWPRM0200	Erect Signage	21	0	26d	19MAR07	12APR07	23APR07	17MAY07																										
Landscape Hardworks																																		
ABWPHL0700	Parapet Wall along Seawall (in ZR)	47	20	23d	21DEC06	08MAR07	21DEC06	04APR07																										
ABWPHL0800	Parapet Wall (in ZK) & N2 (& VO 95 continuation)	22	50	18d	01JAN07	28FEB07	01JAN07	21MAR07																										
ABWPHL0900	Parapet Wall along Seawall (in ZL6)	12	0	18d	30JAN07	12FEB07	29JAN07	08MAR07																										
ABWPHL1000	Parapet Wall along Seawall (in ZL5)	8	0	18d	20JAN07	10FEB07	22FEB07	08MAR07																										
ABWPHL1200	Construct Pergola (3 nos.)	72	90	50d	10APR06	27JAN07	10APR06	30MAR07																										
ABWPHL1300	Water Point WP24-4 to 24-1	15	0	39d	23JAN07	08FEB07	13MAR07	29MAR07																										
ABWPHL1400	Water Point WP23-3 to 22-1	18	0	36d	23JAN07	12FEB07	08MAR07	29MAR07																										
ABWPHL1500	Water Point WP21-3 to 21-1	12	0	2d	02FEB07	15FEB07	05FEB07	21FEB07																										
ABWPHL1600	Water Point WP20-6 to 20-1	21	0	5d	30JAN07	28FEB07	03FEB07	03MAR07																										
ABWPHL1700	Water Point WP19-4 to 19-1	15	0	16d	22JAN07	07FEB07	09FEB07	01MAR07																										
ABWPHL1800	Water Point WP18-3 to 18-2	12	0	19d	22JAN07	03FEB07	13FEB07	01MAR07																										
ABWPHL1900	Water Point WP17-5 to 17-1	18	0	40d	20JAN07	09FEB07	12MAR07	31MAR07																										
ABWPHL2000	Water Point WP16-3 to 16-1	12	0	44d	20JAN07	02FEB07	18MAR07	29MAR07																										
ABWPHL2200	ASD's Contractor Works	303	69	-246d	28JUL06	17MAY07	28JUL06	22JUL06																										
ABWPHL2210	Litter-bin footing excavation (46 nos) (VO179)	10	0	2d	09MAR07	19MAR07	10MAR07	21MAR07																										
ABWPHL2220	Litter-bin footing concreting (46 nos) (VO179)	10	0	2d	20MAR07	30MAR07	22MAR07	02APR07																										
ABWPHL2230	Litter-bin paving temp reinstatement (VO179)	16	0	2d	31MAR07	19APR07	03APR07	21APR07																										
ABWPHL2240	Install litter-bin w/ reinstatement (79 nos S7 & 8)	21	0	0	23APR07	17MAY07	23APR07	17MAY07																										
Section 9																																		
Public Landing Step																																		
Lands Works																																		
A9LSLW0800	Inspection & Testing	30	90	0	01NOV06	23JAN07	01NOV06	23JAN07																										
A9LSLW0900	Fabrication & Painting of Steel Works (Roof)	48	75	2d	05DEC06	06FEB07	05DEC06	08FEB07																										
A9LSLW1000	Concrete Coping with 10 tonne Bollard & Handrail	30	30	3d	13NOV06	13FEB07	13NOV06	16FEB07																										
A9LSLW1400	Public Lighting & Pillar install. (T&C) (VO147)	21	0	0	24JAN07	16FEB07	24JAN07	16FEB07																										
A9LSLW1500	Rubber, Step & land Step Fender	21	0	0	24JAN07	16FEB07	24JAN07	16FEB07																										
A9LSLW1600	Surface Mounted Seats	7	0	2d	07FEB07	14FEB07	09FEB07	16FEB07																										
A9LSLW1700	Construct In situ Concrete Paving	18	5	7d	01NOV06	08FEB07	01NOV06	19FEB07																										

Leader - Wai Kee (C&T) Joint Venture
TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)


start date	10JUN04
finish date	09MAY08
start date	20JAN07
finish date	08FEB07
signature	13A

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point

Act ID	Description	Original Duration	Percent Complete	Total Float	Early Start	Early Finish	Late Start	Late Finish	2006	2007	2008								
										DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	
Area SA6, SA11B & SA14																			
Landscape Softworks																			
BTAASL0600	Soil Mix (In ZS, 400 - North End)	30	21	0	12DEC06 A	16FEB07	12DEC06 A	16FEB07											
BTAASL0800	Planting Works (Section 7 only)	28	0	0	21FEB07	24MAR07	21FEB07	24MAR07											
BTAASL0900	Groundcovers Works	20	0	0	03MAR07	26MAR07	03MAR07	26MAR07											
Section 12																			
Area SA7, SA10, SA11A, SA12 & SA13																			
Landscape Softworks																			
B2ABSL0100	Soil Mix (In ZR, 395m)	47	70	0	21OCT06 A	07FEB07	21OCT06 A	07FEB07											
B2ABSL0200	Soil Mix (In ZK, 180m)	21	0	2d	16FEB07	15MAR07	22FEB07	17MAR07											
B2ABSL0300	Soil Mix (In ZJ6, 85m)	12	0	5d	27FEB07	12MAR07	05MAR07	17MAR07											
B2ABSL0400	Soil Mix (In ZJ5, 50m)	7	0	13d	24JAN07	31JAN07	08FEB07	15FEB07											
B2ABSL0500	Soil Mix (ZJ - Landscape Node 1 South, 260m)	28	50	16d	21DEC06 A	27FEB07	21DEC06 A	17MAR07											
B2ABSL0600	Soil Mix (ZM, ZL1, ZJ)	71	90	51d	21OCT06 A	21FEB07	21OCT06 A	23APR07											
B2ABSL0650	Planting Works for ZR, ZJ5, ZJ6	35	0	22d	08FEB07	23MAR07	09MAR07	19APR07											
B2ABSL0700	Planting Works for ZK, ZJ, ZM, ZL1	40	0	0	23FEB07	11APR07	23FEB07	11APR07											
B2ABSL0800	Groundcovers Works	34	0	0	14MAR07	23APR07	14MAR07	23APR07											
B2ABSL1100	Root Barrier (In ZM & ZJ) (VO/121)	18	90	13d	06NOV06 A	22JAN07	08NOV06 A	06FEB07											
B2ABSL1200	Root Barrier (In ZJ, ZJ5, ZJ6 & ZK) (VO/124)	26	90	13d	13NOV06 A	23JAN07	13NOV06 A	07FEB07											
Section 13																			
Area SA1, SA2, SA3, SA4 & SA6																			
Landscape Softworks																			
B3ACSL0100	Soil Mix (Area SA1 - South Section)	30	28	0	15JAN07 A	16FEB07	15JAN07 A	16FEB07											
B3ACSL0200	Soil Mix (Area SA1 - North Section)	30	30	0	08JAN07 A	21FEB07	08JAN07 A	21FEB07											
B3ACSL0300	Soil Mix (Car Park, Loading & Unloading Area)	6	0	18d	02APR07	09APR07	26APR07	02MAY07											
B3ACSL0400	Soil Mix (Area Adjacent Road SL3)	30	0	7d	09MAR07	13APR07	17MAR07	21APR07											
B3ACSL0500	Planting Works	65	0	0	12FEB07	03MAY07	12FEB07	03MAY07											
B3ACSL0600	Planting Works (Car Park, Loading/Unloading Area)	6	0	18d	10APR07	16APR07	03MAY07	09MAY07											
Area SA8, SA9, SA15, SA16, SA17 & SA18																			
Landscape Softworks																			
B3ADSL0100	Planting Works	35	0	0	22FEB07	03APR07	22FEB07	03APR07											
B3ADSL0200	Groundcovers Works	30	0	0	17MAR07	21APR07	17MAR07	21APR07											
Section 14																			
Area SA6, SA11B & SA14																			
Establishment Works																			
B4ABEW0100	Establishment Works	305	0	0	27MAR07	26MAR08	27MAR07	26MAR08											
Section 15																			
Area SA7, SA10, SA11A, SA12 & SA13																			
Establishment Works																			
B5ABEW0100	Establishment Works	290	0	0	24APR07	04APR08	24APR07	04APR08											
Section 16																			
Area SA1, SA2, SA3, SA4 & SA6																			
Establishment Works																			
B5ACEW0200	Establishment Works	312	0	0	04MAY07	09MAY08	04MAY07	09MAY08											


Start date	10JUN04	End date	09MAY08
Start date	20JAN07	End date	06FEB07
Page number	14A	Page number	14A

Early bar
 Progress bar
 Critical bar
 Summary bar
 Start milestone point



Leader - Wai Kee (C&T) Joint Venture

TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)

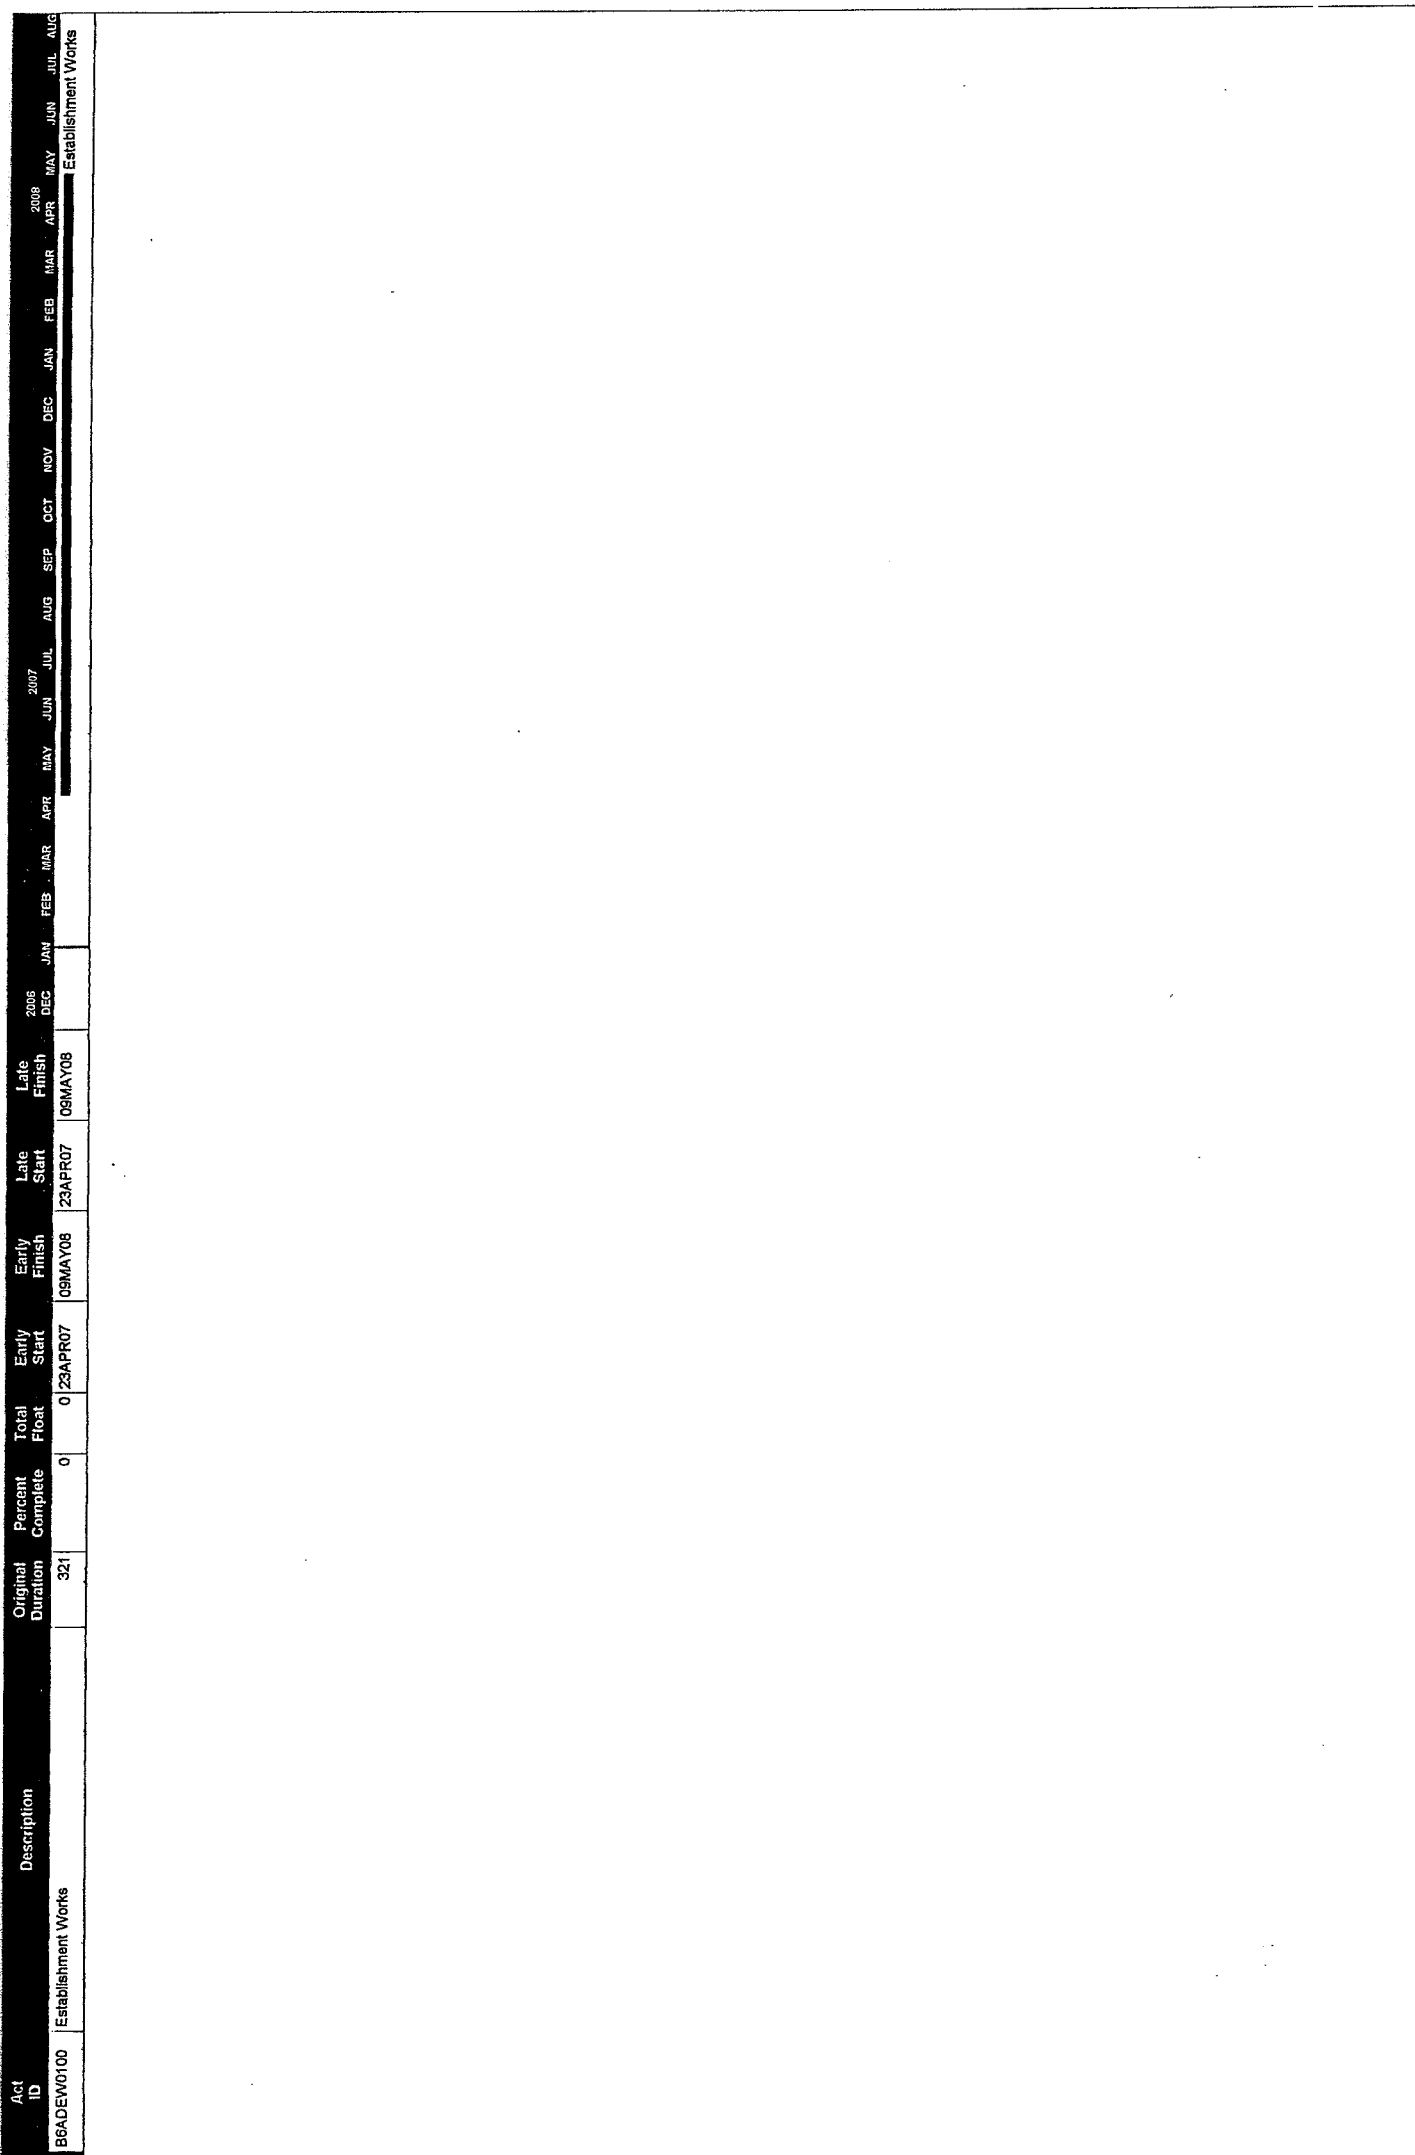

Act ID	Description	Original Duration	Percent Complete	Total Float	2007		2006		2008									
					Early Start	Early Finish	Late Start	Late Finish	APR	MAY	JUN	JUL	AUG					
B0ADEW0100	Establishment Works	321	0	0	23APR07	09MAY08	23APR07	09MAY08										



Start date: 10JUN04
 Finish date: 09MAY08
 Start date: 20JAN07
 Finish date: 06FEB07
 Page number: 15A

Legend:
 [] Early bar
 [] Progress bar
 [] Critical bar
 [] Summary bar
 [] Start milestone point


TP37/03 - Critical Path Reference Program for RP10 (Progress Updated to 20 January 2007)

LEADER



Appendix G

Construction Site Area

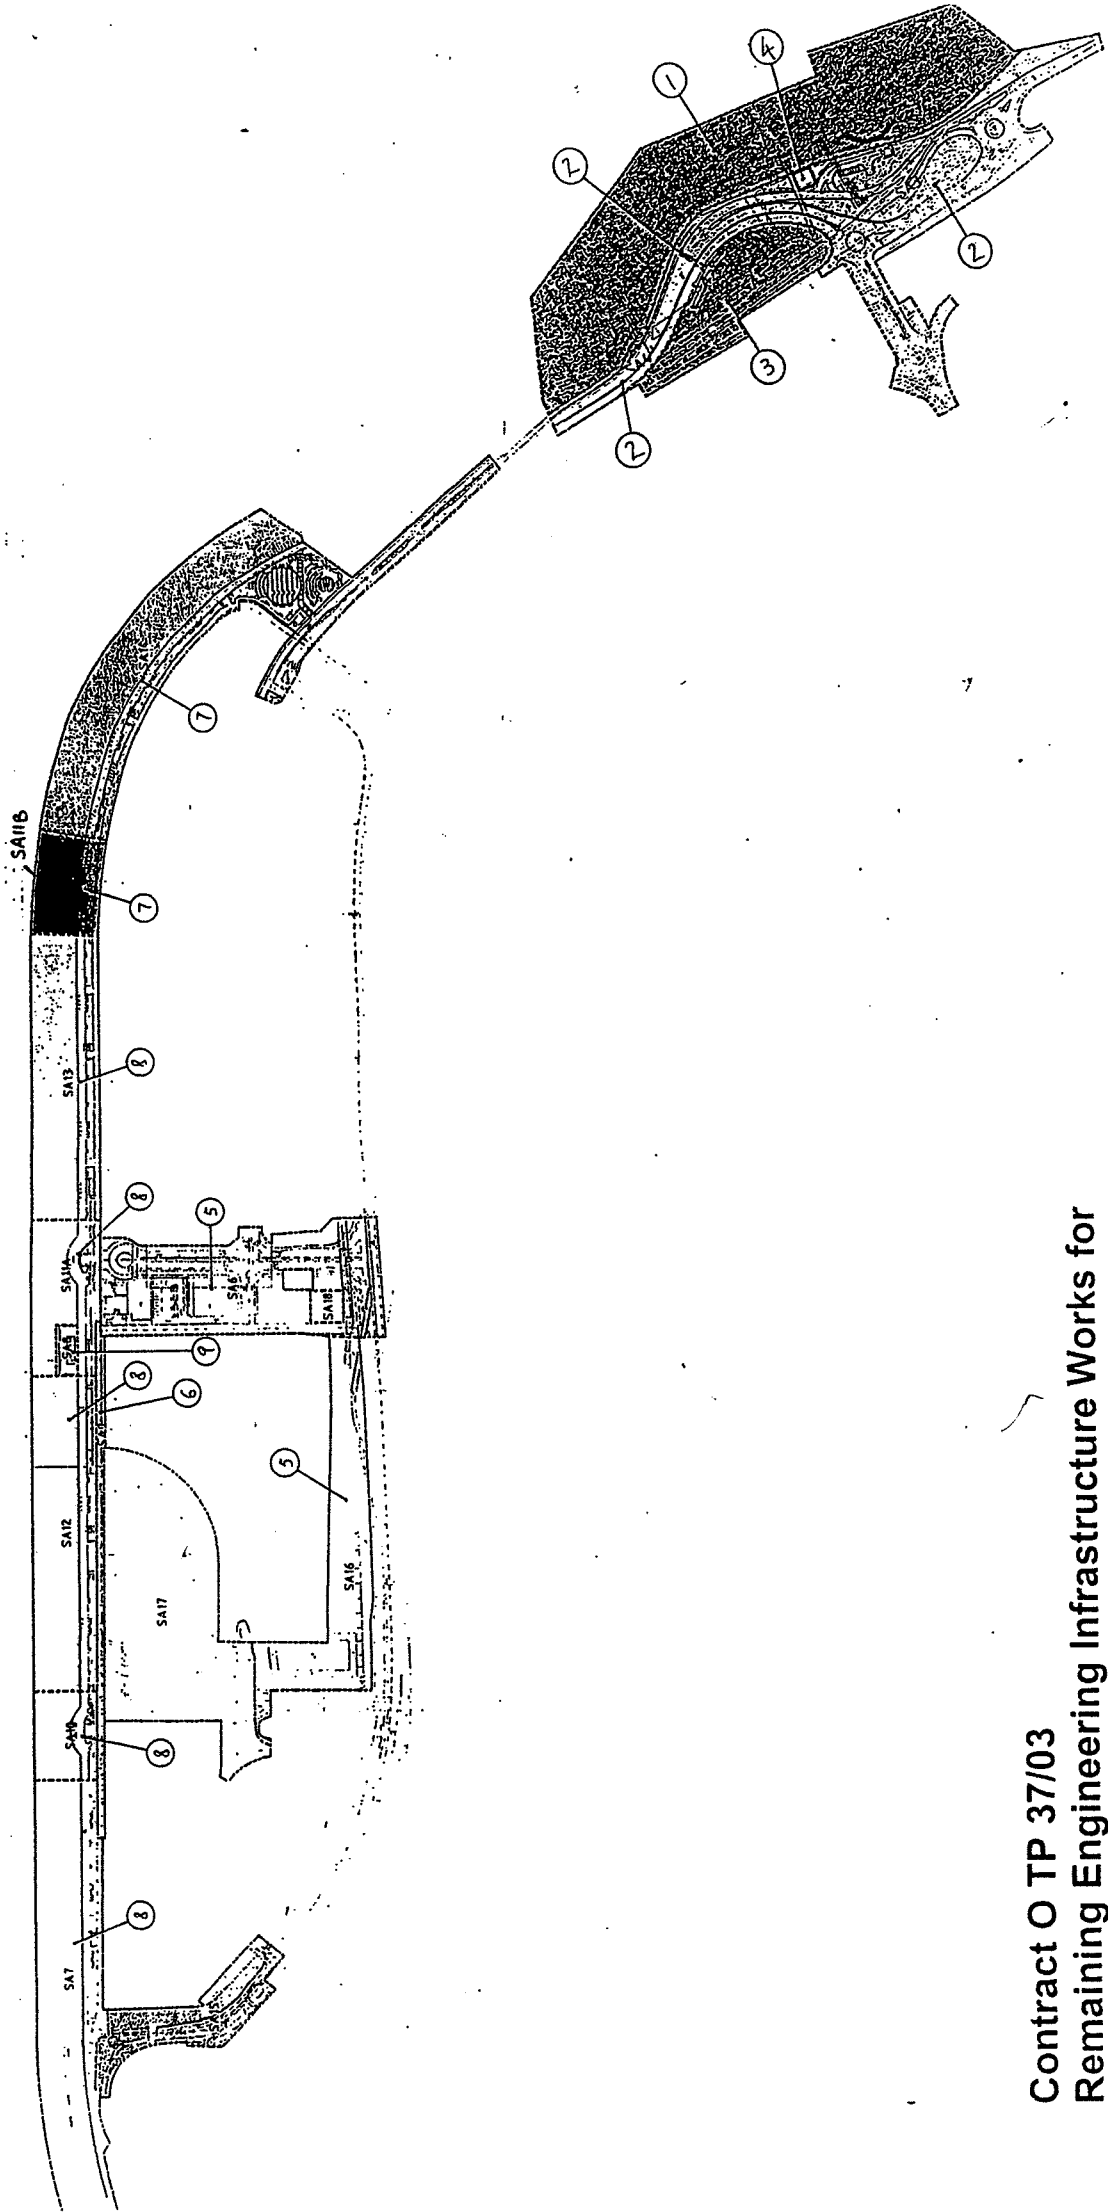

Contract O TP 37/03
 Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2A

Location and Key Pan

Appendix H

**The Implementation Status
of
Mitigation Measures and Follow-up Actions during Weekly
Site Inspections**



Contract No.: TP 37/03 Remaining Engineering Infrastructure Works for
Pak Shek Kok Development Package 2A

SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

Inspection Date : 8 March 2008 Inspected by Name : (RSS) Terry Lau (LWKUN) Wai Tsun (ET) H. T. Chow
 Time : 10:00 Signature : *[Signature]*
 Weather Condition : Sunny / Fine / Overcast / Drizzle / Rain / Storm / Hazy
 Wind : Galm / Light / Breeze / Strong Temperature : 21°C Humidity : High / Moderate / Low

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
Air Quality				
▪ The heights from which fill materials are dropped should be controlled to a practical height to minimize the fugitive dust arising from unloading.	✓			
▪ During transportation by truck, material should be loaded to a level lower than the side and tail boards, and should be dampened or covered before transport.	✓			
▪ All stockpile of aggregate or spoil should be enclosed or covered and water applied in dry or windy condition.		✓		Refer 2
▪ The haul road should be either paved or regular watering.	✓			
▪ Unpaved areas should be watered regularly to avoid dust generation.	✓			
▪ The public road around the site entrance should be kept clean and free from dust.	✓			
▪ Vehicle speed should be limited to 20 km/hr.	✓			
▪ Wheel washing facilities should be provided at all main entrance of work site.	✓			
▪ The enclosures should be around the main dust-generating activities.	✓			
▪ Dusty materials should be sprayed prior to loading.	✓			
▪ All plant and equipment should be well maintained e.g. without black smoke emission.	✓			
▪ Vehicle and equipment should be switched off while not in use.	✓			
▪ Open burning should be prohibited.	✓			
Noise				
▪ The constructions works should be scheduled to minimize noise nuisance.	✓			
▪ Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.	✓			
▪ Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.	✓			
▪ Plant known to emit noise strongly in on direction, should, where possible, be orientated so that the noise is directed away from nearby NSRs.	✓			
▪ Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.	✓			
▪ Noise enclosures, noise barriers, or portable noise barriers used where necessary.	✓			
▪ Air compressors and hand held breakers should have noise labels.	✓			
▪ Compressors and generators should operate with door closed.	✓			
▪ Construction Noise Permits should be available for inspection.	✓			

SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

Mitigation Measures on Waste Management	Implementation Stages*			Remark
	Yes	No	N/A	
Water Quality				
General Construction Activities				
▪ Temporary ditches shall be provided to facilitate runoff discharge into appropriate watercourses, via a sediment trap / sedimentation tanks, prior to discharge.	✓			
▪ Permanent drainage channels shall incorporate sediment basins / traps, and baffles.	✓			
▪ All traps shall incorporate oil and grease removal facilities.	✓			
▪ Sediment traps / sedimentation tanks shall be regular cleaned and maintained regularly.	✓			
▪ All drainage facilities should be adequate for controlled release of storm flows.	✓			
▪ Minimizing of exposed soil areas to reduce the potential for increased siltation and contamination of runoff.	✓			
▪ Open stockpiles of more than 50m ³ should be covered.	✓			
▪ Temporary stockpiles of excavated materials should be covered during rainstorms.	✓			
▪ Manholes should be covered and sealed.	✓			
▪ All chemical stores shall be contained (bunded) such that spills are not allowed to gain access to water bodies.	✓			
▪ Vehicles and plant should be cleaned of earth, mud and debris before leaving the site.	✓			
▪ Vehicle washing facilities should be provided at every site exit.	✓			
▪ Vehicle washing facilities should be adequate to settle out the sand and silt.	✓			
▪ Washing area and road exiting from washing facility should be paved.	✓			
▪ Access road should have sufficient back fall toward washing facility.	✓			
Dredging Activities				
▪ Dredging of designated contaminated marine mud shall only be undertaken by a suitable grab dredger using a close grab.				✓
▪ Mechanical grabs shall be designed and maintained to avoid spillage and shall be seal tightly while being lifted.				✓
▪ All vessels shall be sized such that adequate clearance is maintained between vessel and the sea bed and under water pipelines at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller on the water within the site.				✓
▪ The works shall cause no visible foam, oil, grease, scum litter or other objectionable matter to be present on the water within the site.				✓
▪ All barges shall be fitted with tight fitting seals to their bottom openings to prevent leakage of materials.				✓
▪ Excess material shall be cleaned from the decks and exposed fittings of the barges before the vessels are moved.				✓
▪ Loading of barges shall be controlled to prevent splashing of dredging material to the surrounding water and the barges shall not be filled to a level which will cause overflowing of material or polluted water during loading or transportation.				✓
▪ Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action.				✓

SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
Filling Activities				
▪ Use of silt screen around the filling face to reduce the losses to the surrounding.				
▪ All vessels shall be sized such that adequate clearance is maintained between vessel and the sea bed and under water pipeline at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash or pipelines damaged.			✓	
▪ The works shall cause no visible foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site.			✓	
▪ All barges shall be fitted with tight fitting seals to their bottom openings to prevent leakage of material.			✓	
▪ Loading of barges shall be controlled to prevent splashing of dredged material to the surrounding water and barges shall not be filled to a level which will cause overflowing of material or polluted water during loading transportation.			✓	
Waste Management				
Marine Dredged Sediment				
• Relevant licence / permits for disposal of marine dredged sediment are available for inspection.			✓	
• Bottom opening of barges is fitted with tight fitting seals to prevent leakage of material. Excess material is cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.			✓	
• Monitoring of the barging loading is conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels are equipped with automatic self-monitoring devices as specified by the EPD.			✓	
• Transport of dredged marine sediments to the disposal site is by split barge of not less than 750m ³ capacity, well maintained and capable of rapid opening and discharge at the disposal site.			✓	
• Inspection of the barge loading to ensure that loss of material does not take place during transportation.			✓	
Construction and Demolition (C&D) Waste				
• Most of the C&D materials generated from the construction are sorted immediately in-situ to find out if they can be re-used for this job site or for other job sites.	✓			
• Sufficient spaces are identified and provided during the construction stage for the collection, temporary storage and on-site sorting of C&D materials.	✓			
• Proper protective measures, such as fences and tarpaulin, are provided, in order to protect the temporary stockpiled materials for later reuse / recycle.	✓			
• Avoiding cross contamination to reusable and / or recyclable materials collected (e.g. covering the reusable materials)	✓			
• In order to reduce the impacts to the public, except for those sorted inert C&D materials to be reused on site, all other sorted non-inert materials (e.g. general refuse and waste formworks) shall be removed off site as soon as practicable in order to optimise the use of the on-site storage space. If the non-inert materials need to be stored on site for a short period, the materials shall be centralized and stored at specific areas far away the sensitive receivers.	✓			
• All Public Fill arising from the demolition works shall be limited to a size not more than 250mm and free of reinforcement bars, timber, etc. before re-using it.	✓			
• Recyclable materials sorted from the site should be collected by potential recycling contractors under the Contractor's arrangement.	✓			
• Trip ticket system will be implemented to ensure proper waste disposal at public filling and landfills	✓			
• Appropriate measures should be employed to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	✓			
• Proper resource planning and calculations before ordering the construction materials to be used will ensure that the wastage of the materials can be minimized	✓			




SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*		Remark
	Yes	No / N/A	
Mitigation Measures on Waste Management			
• Proper storage will minimize the damage and thus the wastage of the materials	✓		
• Training of site personnel in proper waste management procedures. The workers shall be constantly educated for the awareness of the proper handling of waste and to reduce the amount of waste while Site Agent shall be constantly met to discuss the effectiveness of the implementation of the waste management plan. Information to promote the waste management and the reduction concept shall be posted at the site to raise alertness of the personnel concerned.	✓		
• Chemical Waste			
• It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	✓		
• After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	✓		
• Chemical wastes should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.	✓		
• Containers used for the storage of chemical wastes			
• Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed	✓		
• Have a capacity of less than 450L unless the specification have been approved by the EPD	✓		
• Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Chemical Waste (General) Regulations and Codes of Practice	✓		
• Labelling			
• Every container of chemical waste would bear an appropriate label, which would contain the particulars details.	✓		
• The waste produced would ensure that the information contained on the label is accurate and sufficient so as to enable proper and safe handling, storage and transport of the chemical waste	✓		
• Storage Area			
• Be clearly labeled and used solely for the storage of chemical waste	✓		
• Be enclosed on at least 3 sides	✓		
• Have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest	✓		
• Have adequate ventilation	✓		
• Be covered to prevent rainfall entering	✓		
• Be arranged so that incompatible materials are adequately separated	✓		
• Be clean and maintain regularly	✓		
• Disposal			
• Be via a licensed waste collector	✓		
• To a licensed disposal facility, such as Chemical Waste Treatment Centre	✓		
• Be a reuser of the waste, under approval from the EPD	✓		



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
• Spillage				
• Establish source of spill or discharge and determine nature of material, where possible halt discharge	✓			
• Commencing at the source of the spill, establish all current and potential impacted areas	✓			
• Commence containment of spill using bunds made from available materials and ground water cut-off trenches where necessary	✓			
• After spill is contained remove material (including contaminated soil where necessary) using pumps and/or absorbent materials	✓			
• Dispose of materials as chemical wastes	✓			
• General Refuse				
• General refuse generated on-site is in enclosed bins or compaction units separate from construction and chemical waste	✓			
• A reputable waste collector is employed by the Contractor to remove general refuse from the site, separately from the construction and chemical waste.	✓			
• General refuse generated is removed on daily or every second day basis to minimise odour, pest and litter impacts	✓			
• Aluminium cans are recovered from the waste stream by individual collectors if they are segregated or easily accessible, so separate, labelled bins for their deposit should be provided if feasible.	✓			
• Office wastes are reduced through recycling of paper if volumes are large enough to warrant collection.	✓			
• Site Practice				
• Good site practices should be adopted to clean the rubbish and litter on the construction sites so as to prevent the rubbish and litter from dropping into the nearby environment. Construction sites should be cleaned on a regular basis.	✓			
• The Contractor assigned worker is responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	✓			
• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.	✓			
• The Environmental Permit should be displaced conspicuously on site	✓			
• Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	✓			
• Any unused chemicals or those with remaining functional capacity should be recycled.	✓			
• A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.	✓			
• Suitable collection sites around site offices will be required. For environmental hygiene reasons and to minimize odor, refuse should not be stored for a period exceeding 48 hours, however, removal every 24 hours is preferable.	✓			
• Minimize windblown litter and dust during transportation by either covering trucks or transporting wastes in enclosed container.	✓			
• All generators, fuel and oil storage are within bundle areas.	✓			
• Oil leakage from machinery, vehicle and plant is prevented.	✓			
• Chemical storage area, drainage systems, silt traps, sumps and oil interceptors are cleaned and maintained regularly.	✓			

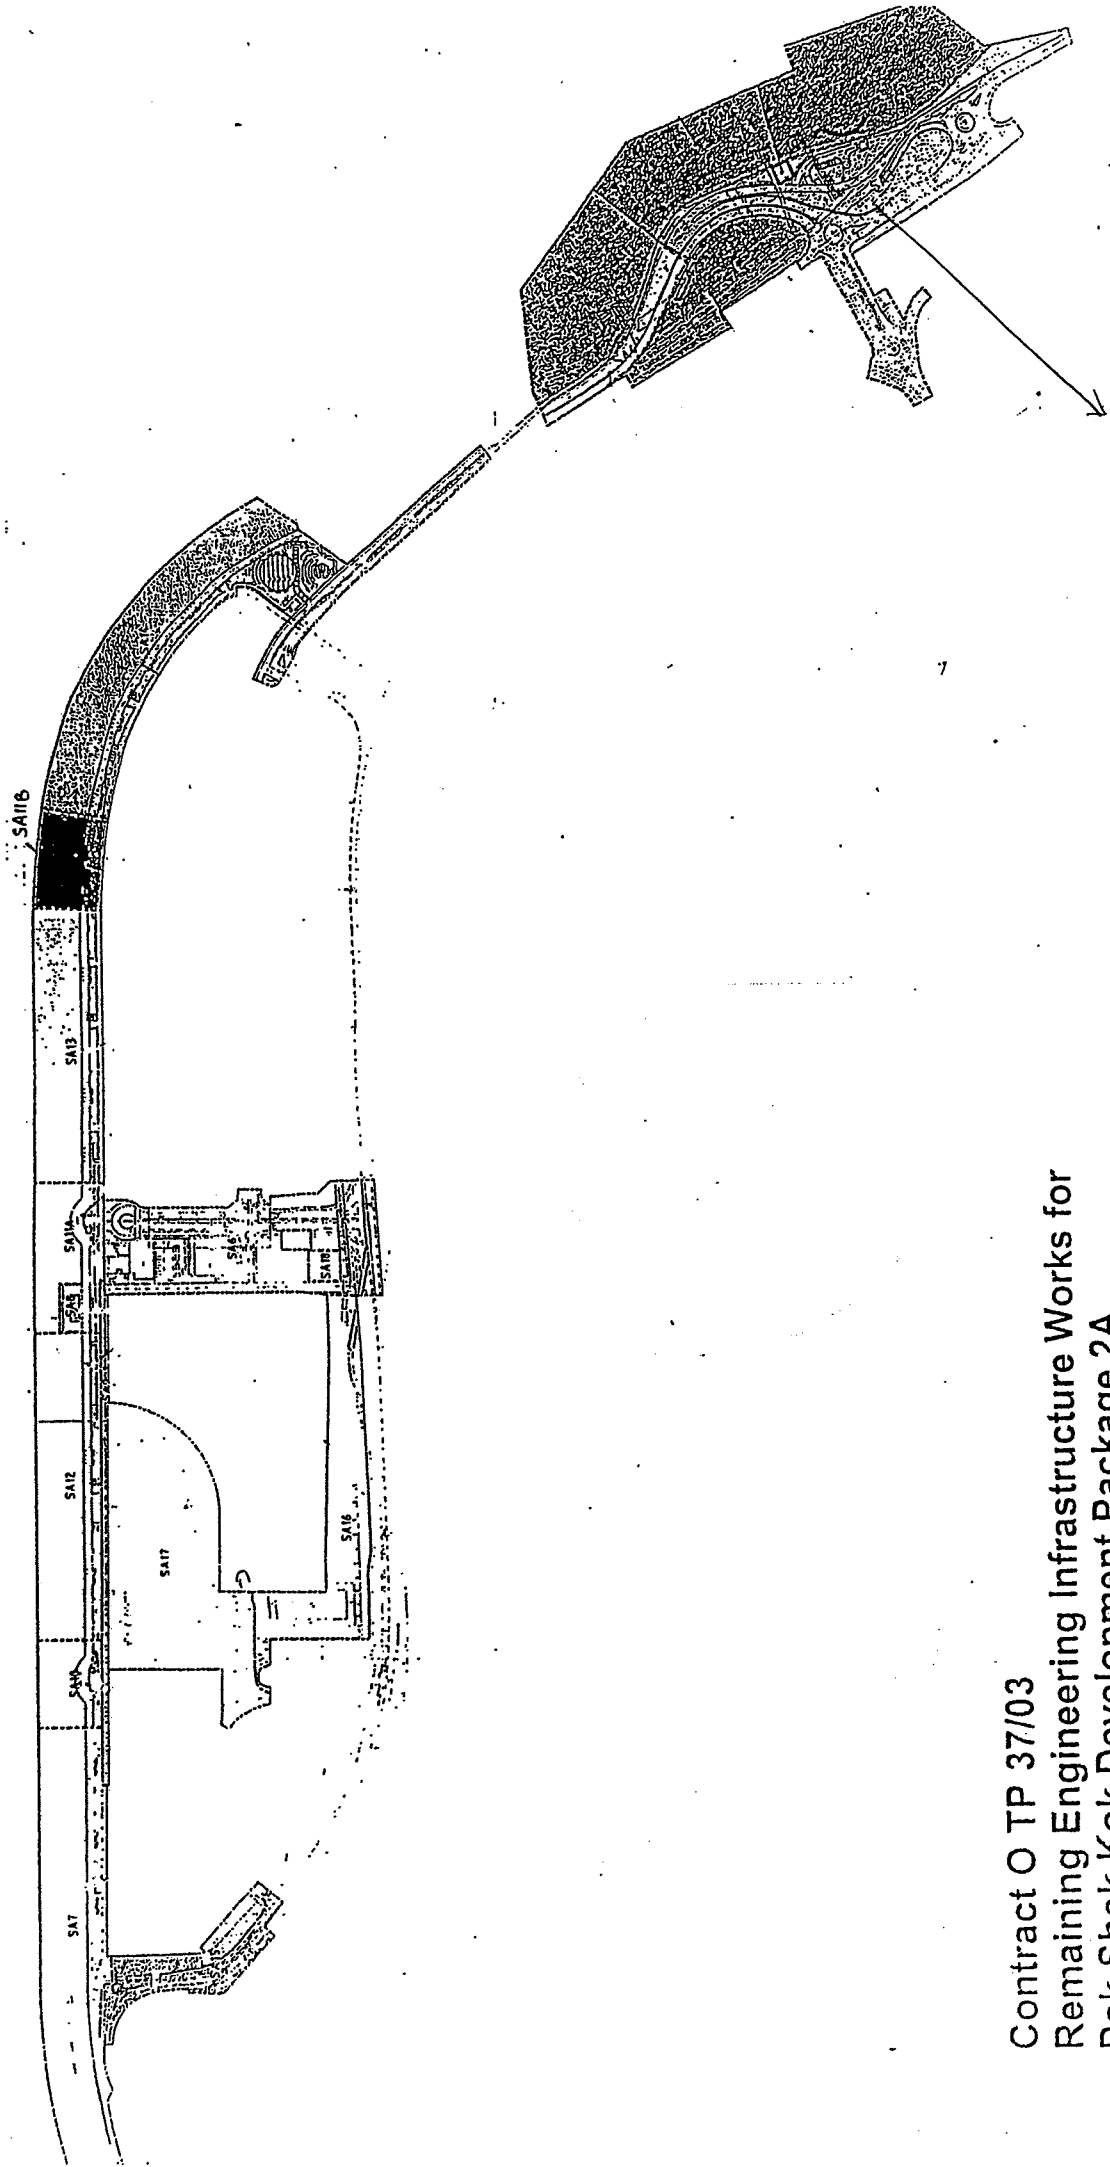



Item 2 (Avoid Abutment.)

Contract O TP 37/03
 Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2A

Location and Key Plan

Table for follow-up Action:

Item	Details of defective works or observations	Location	Further action to be taken (Included persons / party to take action)	Expected Date for Action taken
1.	Follow up action to the previous site inspections item ① on 25-1-08, item ② on 2-2-08, item ③ on 6-2-08, item ④ on 16-2-08, item ⑤ on 23-2-08, item ⑥ on 28-2-08, pesticide was applied in drainage channel and temporary ditches.	Void Abutment	Follow up action was completed, no further action to be taken.	N/A
2.	Follow up action to the previous site inspection item ③ on 28-2-2008, stockpile of sand was still noted at Void Abutment without covered.	Void Abutment	The Contract was reminded to cover the stockpile of spray prior to loading.	15-3-2008

Signature:		RSS		LWKJV	ET
Name:	Terry Law		Wai T. Chow		
Date:	8 March 08		8 March 2008		

Contract No.: TP 3703 Remaining Engineering Infrastructure Works for
Pak Shek Kok Development Package 2A

SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

Inspection Date : 15 March 2008 Inspected by Name : (RSS) Michelle Fung. (LWKJM) Inspection Station (ET) H. T. Chow
 Time : 10:30 Signature : *[Signature]*
 Weather Condition Wind : Sunny / Fine / Overcast / Drizzle / Rain / Storm / Heavy Storm / Hazy
 Temperature : 24°C
 Humidity : High / Moderate / Low

	Implementation Stages*			Remark
	Yes	No	N/A	
Air Quality				
▪ The heights from which fill materials are dropped should be controlled to a practical height to minimize the fugitive dust arising from unloading.	✓			
▪ During transportation by truck, material should be loaded to a level lower than the side and tail boards, and should be dampened or covered before transport.	✓			
▪ All stockpile of aggregate or spoil should be enclosed or covered and water applied in dry or windy condition.	✓			
▪ The haul road should be either paved or regular watering.	✓			
▪ Unpaved areas should be watered regularly to avoid dust generation.	✓			
▪ The public road around the site entrance should be kept clean and free from dust.	✓			
▪ Vehicle speed should be limited to 20 km/hr.	✓			
▪ Wheel washing facilities should be provided at all main entrance of work site.	✓			
▪ The enclosures should be around the main dust-generating activities.	✓			
▪ Dusty materials should be sprayed prior to loading.	✓			
▪ All plant and equipment should be well maintained e.g. without black smoke emission.	✓			
▪ Vehicle and equipment should be switched off while not in use.	✓			
▪ Open burning should be prohibited.	✓			
Noise				
▪ The constructions works should be scheduled to minimize noise nuisance.	✓			
▪ Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.	✓			
▪ Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.	✓			
▪ Plant known to emit noise strongly in on direction, should, where possible, be orientated so that the noise is directed away from nearby NSRs.	✓			
▪ Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.	✓			
▪ Noise enclosures, noise barriers, or portable noise barriers used where necessary.	✓			
▪ Air compressors and hand held breakers should have noise labels.	✓			
▪ Compressors and generators should operate with door closed.	✓			
▪ Construction Noise Permits should be available for inspection.	✓			



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

Mitigation Measures on Waste Management	Implementation Stages*			Remark
	Yes	No	N/A	
Water Quality				
General Construction Activities				
Temporary ditches shall be provided to facilitate runoff discharge into appropriate watercourses, via a sediment trap / sedimentation tanks, prior to discharge.	✓			
Permanent drainage channels shall incorporate sediment basins / traps, and baffles.	✓			
All traps shall incorporate oil and grease removal facilities.	✓			
Sediment traps / sedimentation tanks shall be regular cleaned and maintained regularly.	✓			
All drainage facilities should be adequate for controlled release of storm flows.	✓			
Minimizing of exposed soil areas to reduce the potential for increased siltation and contamination of runoff.	✓			
Open stockpiles of more than 50m ³ should be covered.	✓			
Temporary stockpiles of excavated materials should be covered during rainstorms.	✓			
Manholes should be covered and sealed.	✓			
All chemical stores shall be contained (bunded) such that spills are not allowed to gain access to water bodies.	✓			
Vehicles and plant should be cleaned of earth, mud and debris before leaving the site.	✓			
Vehicle washing facilities should be provided at every site exit.	✓			
Vehicle washing facilities should be adequate to settle out the sand and silt.	✓			
Washing area and road exiting from washing facility should be paved.	✓			
Access road should have sufficient back fall toward washing facility.	✓			
Dredging Activities				
Dredging of designated contaminated marine mud shall only be undertaken by a suitable grab dredger using a close grab.			✓	
Mechanical grabs shall be designed and maintained to avoid spillage and shall be seal tightly while being lifted.			✓	
All vessels shall be sized such that adequate clearance is maintained between vessel and the sea bed and under water pipelines at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller on the water within the site.			✓	
The works shall cause no visible foam, oil, grease, scum litter or other objectionable matter to be present on the water within the site.			✓	
All barges shall be fitted with tight fitting seals to their bottom openings to prevent leakage of materials.			✓	
Excess material shall be cleaned from the decks and exposed fittings of the barges before the vessels are moved.			✓	
Loading of barges shall be controlled to prevent splashing of dredging material to the surrounding water and the barges shall not be filled to a level which will cause overflowing of material or polluted water during loading or transportation.			✓	
Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action.			✓	



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
Filling Activities				
▪ Use of silt screen around the filling face to reduce the losses to the surrounding.			✓	
▪ All vessels shall be sized such that adequate clearance is maintained between vessel and the sea bed and under water pipeline at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash or pipelines damaged.			✓	
▪ The works shall cause no visible foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site.			✓	
▪ All barges shall be fitted with tight fitting seals to their bottom openings to prevent leakage of material.			✓	
▪ Loading of barges shall be controlled to prevent splashing of dredged material to the surrounding water and barges shall not be filled to a level which will cause overflowing of material or polluted water during loading transportation.			✓	
Waste Management				
Marine Dredged Sediment				
• Relevant licence / permits for disposal of marine dredged sediment are available for inspection.			✓	
• Bottom opening of barges is fitted with tight fitting seals to prevent leakage of material. Excess material is cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.			✓	
• Monitoring of the barging loading is conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels are equipped with automatic self-monitoring devices as specified by the EPD.			✓	
• Transport of dredged marine sediments to the disposal site is by split barge of not less than 750m ³ capacity, well maintained and capable of rapid opening and discharge at the disposal site.			✓	
• Inspection of the barge loading to ensure that loss of material does not take place during transportation.			✓	
Construction and Demolition (C&D) Waste				
• Most of the C&D materials generated from the construction are sorted immediately in-situ to find out if they can be re-used for this job site or for other job sites.	✓			
• Sufficient spaces are identified and provided during the construction stage for the collection, temporary storage and on-site sorting of C&D materials.	✓			
• Proper protective measures, such as fences and tarpaulin, are provided, in order to protect the temporary stockpiled materials for later reuse / recycle.	✓			
• Avoiding cross contamination to reusable and / or recyclable materials collected (e.g. covering the reusable materials)	✓			
• In order to reduce the impacts to the public, except for those sorted inert C&D materials to be reused on site, all other sorted non-inert materials (e.g. general refuse and waste formworks) shall be removed off site as soon as practicable in order to optimise the use of the on-site storage space. If the non-inert materials need to be stored on site for a short period, the materials shall be centralized and stored at specific areas far away the sensitive receivers.	✓			
• All Public Fill arising from the demolition works shall be limited to a size not more than 250mm and free of reinforcement bars, timber, etc. before re-using it.	✓			
• Recyclable materials sorted from the site should be collected by potential recycling contractors under the Contractor's arrangement.	✓			
• Trip ticket system will be implemented to ensure proper waste disposal at public filling and landfills	✓			
• Appropriate measures should be employed to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	✓			
• Proper resource planning and calculations before ordering the construction materials to be used will ensure that the wastage of the materials can be minimized	✓			




SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
• Proper storage will minimize the damage and thus the wastage of the materials	✓			
• Training of site personnel in proper waste management procedures. The workers shall be constantly educated for the awareness of the proper handling of waste and to reduce the amount of waste while Site Agent shall be constantly met to discuss the effectiveness of the implementation of the waste management plan. Information to promote the waste management and the reduction concept shall be posted at the site to raise alertness of the personnel concerned.	✓			
• Chemical Waste				
• It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	✓			
• After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.		✓		16m 3
• Chemical wastes should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.	✓			
• Containers used for the storage of chemical wastes				
• Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed	✓			
• Have a capacity of less than 450L unless the specification have been approved by the EPD	✓			
• Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Chemical Waste (General) Regulations and Codes of Practice	✓			
• Labelling				
• Every container of chemical waste would bear an appropriate label, which would contain the particulars details.	✓			
• The waste produced would ensure that the information contained on the label is accurate and sufficient so as to enable proper and safe handling, storage and transport of the chemical waste	✓			
• Storage Area				
• Be clearly labeled and used solely for the storage of chemical waste	✓			
• Be enclosed on at least 3 sides	✓			
• Have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest	✓			
• Have adequate ventilation	✓			
• Be covered to prevent rainfall entering	✓			
• Be arranged so that incompatible materials are adequately separated	✓			
• Be clean and maintain regularly	✓			
• Disposal				
• Be via a licensed waste collector	✓			
• To a licensed disposal facility, such as Chemical Waste Treatment Centre	✓			
• Be a reuser of the waste, under approval from the EPD	✓			



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Mitigation Measures on Waste Management	Implementation Stages*			Remark
		Yes	No	N/A	
		Spillage			
•	Establish source of spill or discharge and determine nature of material, where possible halt discharge				
•	Commencing at the source of the spill, establish all current and potential impacted areas				
•	Commence containment of spill using bunds made from available materials and ground water cut-off trenches where necessary				
•	After spill is contained remove material (including contaminated soil where necessary) using pumps and/or absorbent materials				
•	Dispose of materials as chemical wastes				
•	General Refuse				
•	General refuse generated on-site is in enclosed bins or compaction units separate from construction and chemical waste	✓			
•	A reputable waste collector is employed by the Contractor to remove general refuse from the site, separately from the construction and chemical waste.	✓			
•	General refuse generated is removed on daily or every second day basis to minimise odour, pest and litter impacts	✓			
•	Aluminium cans are recovered from the waste stream by individual collectors if they are segregated or easily accessible, so separate, labelled bins for their deposit should be provided if feasible.	✓			
•	Office wastes are reduced through recycling of paper if volumes are large enough to warrant collection.	✓			
•	Site Practice				
•	Good site practices should be adopted to clean the rubbish and litter on the construction sites so as to prevent the rubbish and litter from dropping into the nearby environment. Construction sites should be cleaned on a regular basis.	✓			
•	The Contractor assigned worker is responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	✓			
•	Proper storage and site practices to minimise the potential for damage or contamination of construction materials.	✓			
•	The Environmental Permit should be displaced conspicuously on site	✓			
•	Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	✓			
•	Any unused chemicals or those with remaining functional capacity should be recycled.	✓			
•	A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.	✓			
•	Suitable collection sites around site offices will be required. For environmental hygiene reasons and to minimize odor, refuse should not be stored for a period exceeding 48 hours, however, removal every 24 hours is preferable.	✓			
•	Minimize windblown litter and dust during transportation by either covering trucks or transporting wastes in enclosed container.	✓			
•	All generators, fuel and oil storage are within bundle areas.	✓			
•	Oil leakage from machinery, vehicle and plant is prevented.	✓			
•	Chemical storage area, drainage systems, silt traps, sumps and oil interceptors are cleaned and maintained regularly.	✓			

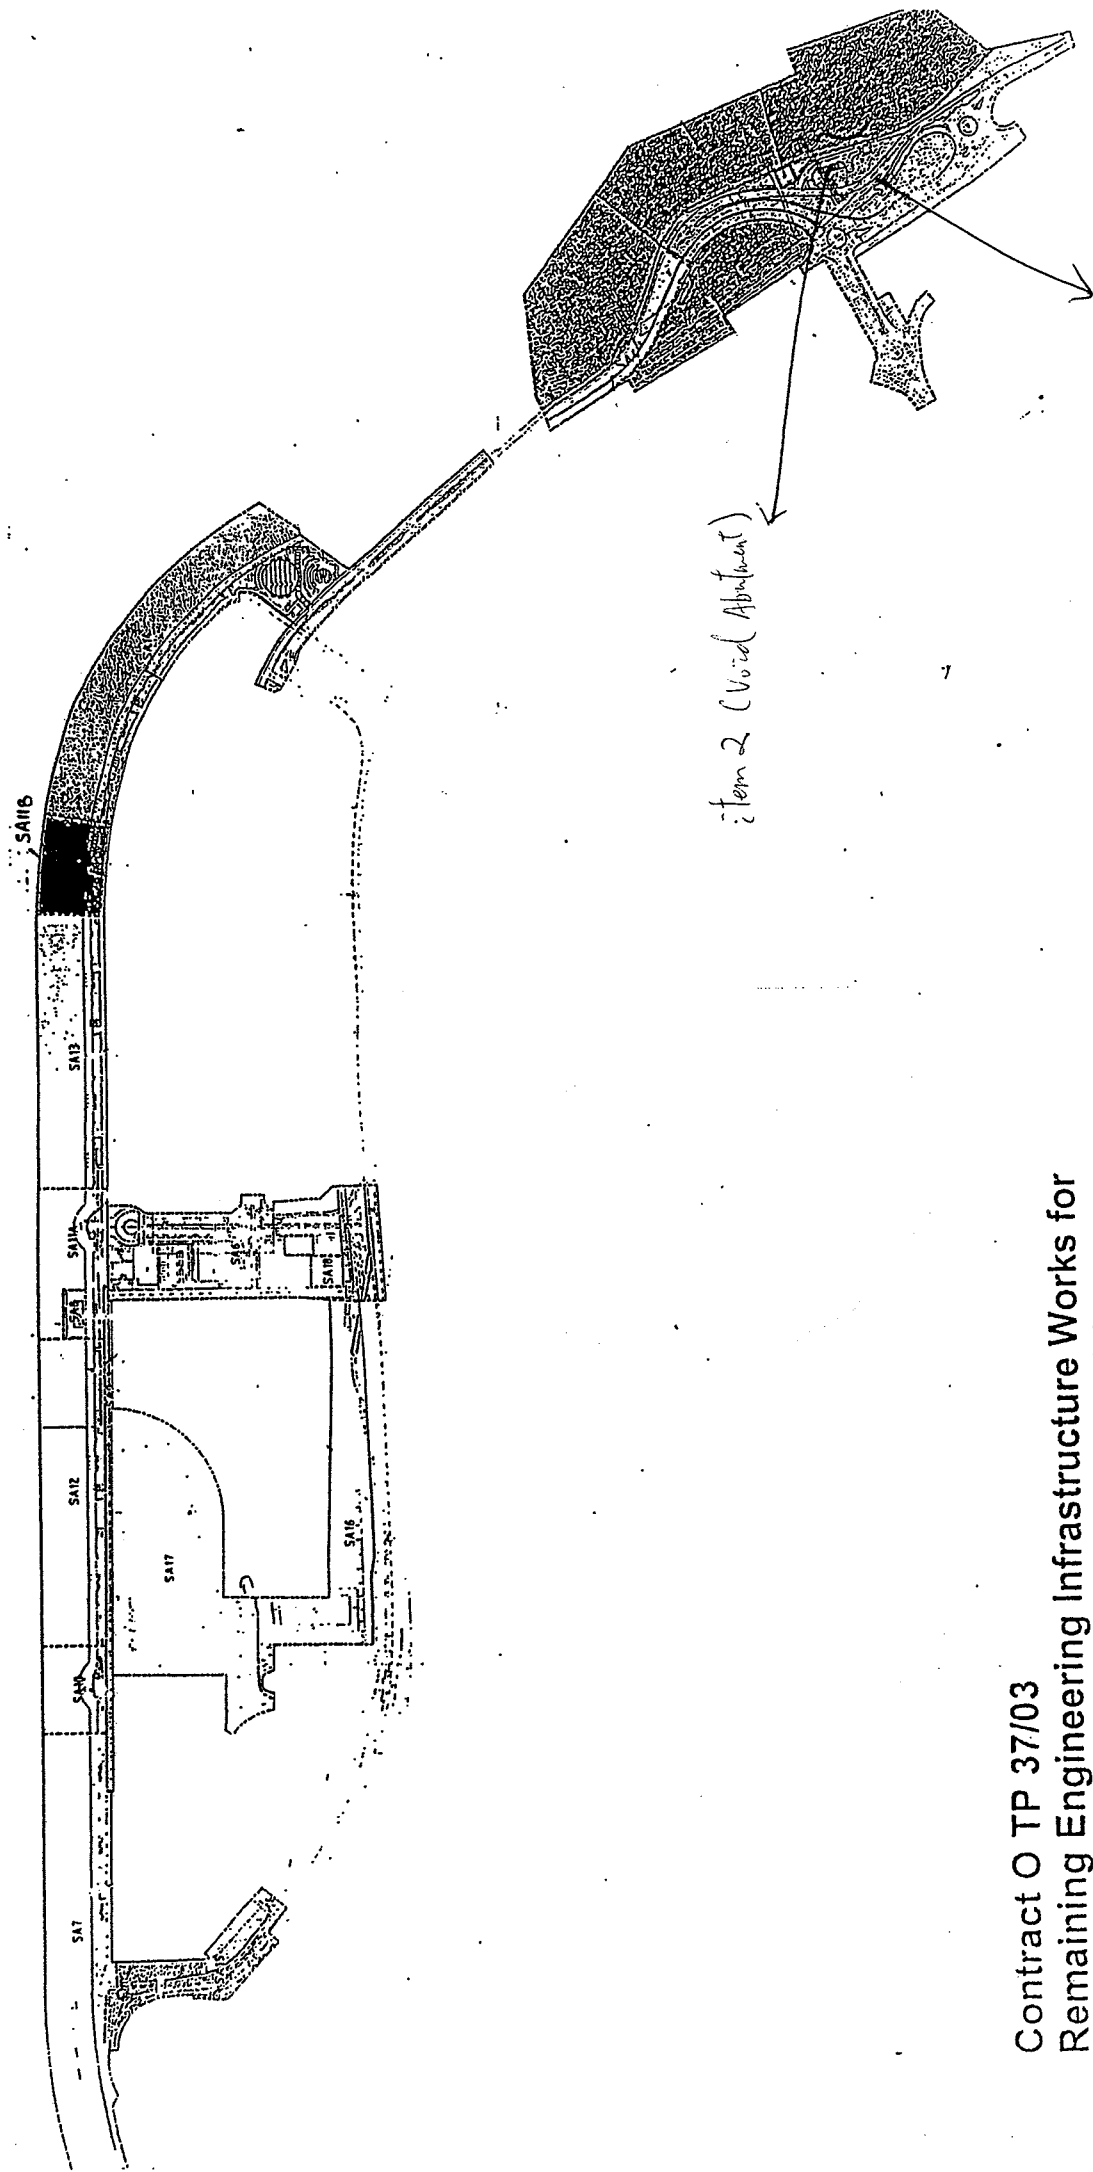

Item 2 (Void Abutment)

Item 3 (Void Abutment)

Contract O TP 37/03
 Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2A

Location and Key Plan

Contract No.: TP 37/03 Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2A

SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

Inspection Date : 20 March 2008 Inspected by Name : (RSS) Terry Law (LWKJN) Wai Koon Chan (ET) M. T. Chow
 Time : 10:30 Signature : 

Weather Condition : Sunny / Fine / Overcast / ~~Drizzle~~ / ~~Rain~~ / ~~Storm~~ / ~~Heavy~~
 Wind : ~~Calm~~ / ~~Light~~ / Breeze / ~~Strong~~ Temperature : 21°C Humidity : High / Moderate / Low

	Implementation Stages*			Remark
	Yes	No	N/A	
Air Quality				
▪ The heights from which fill materials are dropped should be controlled to a practical height to minimize the fugitive dust arising from unloading.	<input checked="" type="checkbox"/>			
▪ During transportation by truck, material should be loaded to a level lower than the side and tail boards, and should be dampened or covered before transport.	<input checked="" type="checkbox"/>			
▪ All stockpile of aggregate or spoil should be enclosed or covered and water applied in dry or windy condition.	<input checked="" type="checkbox"/>			
▪ The haul road should be either paved or regular watering.	<input checked="" type="checkbox"/>			
▪ Unpaved areas should be watered regularly to avoid dust generation.	<input checked="" type="checkbox"/>			
▪ The public road around the site entrance should be kept clean and free from dust.	<input checked="" type="checkbox"/>			
▪ Vehicle speed should be limited to 20 km/hr.	<input checked="" type="checkbox"/>			
▪ Wheel washing facilities should be provided at all main entrance of work site.	<input checked="" type="checkbox"/>			
▪ The enclosures should be around the main dust-generating activities.	<input checked="" type="checkbox"/>			
▪ Dusty materials should be sprayed prior to loading.	<input checked="" type="checkbox"/>			
▪ All plant and equipment should be well maintained e.g. without black smoke emission.	<input checked="" type="checkbox"/>			
▪ Vehicle and equipment should be switched off while not in use.	<input checked="" type="checkbox"/>			
▪ Open burning should be prohibited.	<input checked="" type="checkbox"/>			
Noise				
▪ The constructions works should be scheduled to minimize noise nuisance.	<input checked="" type="checkbox"/>			
▪ Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.	<input checked="" type="checkbox"/>			
▪ Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.	<input checked="" type="checkbox"/>			
▪ Plant known to emit noise strongly in on direction, should, where possible, be orientated so that the noise is directed away from nearby NSRs.	<input checked="" type="checkbox"/>			
▪ Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.	<input checked="" type="checkbox"/>			
▪ Noise enclosures, noise barriers, or portable noise barriers used where necessary.	<input checked="" type="checkbox"/>			
▪ Air compressors and hand held breakers should have noise labels.	<input checked="" type="checkbox"/>			
▪ Compressors and generators should operate with door closed.	<input checked="" type="checkbox"/>			
▪ Construction Noise Permits should be available for inspection.	<input checked="" type="checkbox"/>			

SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
Water Quality				
General Construction Activities				
▪ Temporary ditches shall be provided to facilitate runoff discharge into appropriate watercourses, via a sediment trap / sedimentation tanks, prior to discharge.	✓			
▪ Permanent drainage channels shall incorporate sediment basins / traps, and baffles.	✓			
▪ All traps shall incorporate oil and grease removal facilities.	✓			
▪ Sediment traps / sedimentation tanks shall be regular cleaned and maintained regularly.	✓			
▪ All drainage facilities should be adequate for controlled release of storm flows.	✓			
▪ Minimizing of exposed soil areas to reduce the potential for increased siltation and contamination of runoff.	✓			
▪ Open stockpiles of more than 50m ³ should be covered.	✓			
▪ Temporary stockpiles of excavated materials should be covered during rainstorms.	✓			
▪ Manholes should be covered and sealed.	✓			
▪ All chemical stores shall be contained (bunded) such that spills are not allowed to gain access to water bodies.	✓			
▪ Vehicles and plant should be cleaned of earth, mud and debris before leaving the site.	✓			
▪ Vehicle washing facilities should be provided at every site exit.	✓			
▪ Vehicle washing facilities should be adequate to settle out the sand and silt.	✓			
▪ Washing area and road exiting from washing facility should be paved.	✓			
▪ Access road should have sufficient back fall toward washing facility.	✓			
Dredging Activities				
▪ Dredging of designated contaminated marine mud shall only be undertaken by a suitable grab dredger using a close grab.			✓	
▪ Mechanical grabs shall be designed and maintained to avoid spillage and shall be seal tightly while being lifted.			✓	
▪ All vessels shall be sized such that adequate clearance is maintained between vessel and the sea bed and under water pipelines at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller on the water within the site.			✓	
▪ The works shall cause no visible foam, oil, grease, scum litter or other objectionable matter to be present on the water within the site.			✓	
▪ All barges shall be fitted with tight fitting seals to their bottom openings to prevent leakage of materials.			✓	
▪ Excess material shall be cleaned from the decks and exposed fittings of the barges before the vessels are moved.			✓	
▪ Loading of barges shall be controlled to prevent splashing of dredging material to the surrounding water and the barges shall not be filled to a level which will cause overflowing of material or polluted water during loading or transportation.			✓	
▪ Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action.			✓	



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Mitigation Measures on Waste Management	Implementation Stages*			Remark
		Yes	No	N/A	
Filling Activities					
▪	Use of silt screen around the filling face to reduce the losses to the surrounding.				
▪	All vessels shall be sized such that adequate clearance is maintained between vessel and the sea bed and under water pipeline at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash or pipelines damaged.				
▪	The works shall cause no visible foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site.				
▪	All barges shall be fitted with tight fitting seals to their bottom openings to prevent leakage of material.				
▪	Loading of barges shall be controlled to prevent splashing of dredged material to the surrounding water and barges shall not be filled to a level which will cause overflowing of material or polluted water during transportation.				
Waste Management					
Marine Dredged Sediment					
•	Relevant licence / permits for disposal of marine dredged sediment are available for inspection.				
•	Bottom opening of barges is fitted with tight fitting seals to prevent leakage of material. Excess material is cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.				
•	Monitoring of the barging loading is conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels are equipped with automatic self-monitoring devices as specified by the EPD.				
•	Transport of dredged marine sediments to the disposal site is by split barge of not less than 750m ³ capacity, well maintained and capable of rapid opening and discharge at the disposal site.				
•	Inspection of the barge loading to ensure that loss of material does not take place during transportation.				
Construction and Demolition (C&D) Waste					
•	Most of the C&D materials generated from the construction are sorted immediately in-situ to find out if they can be re-used for this job site or for other job sites.	✓			
•	Sufficient spaces are identified and provided during the construction stage for the collection, temporary storage and on-site sorting of C&D materials.	✓			
•	Proper protective measures, such as fences and tarpaulin, are provided, in order to protect the temporary stockpiled materials for later reuse / recycle.	✓			
•	Avoiding cross contamination to reusable and / or recyclable materials collected (e.g. covering the reusable materials)	✓			
•	In order to reduce the impacts to the public, except for those sorted inert C&D materials to be reused on site, all other sorted non-inert materials (e.g. general refuse and waste formworks) shall be removed off site as soon as practicable in order to optimise the use of the on-site storage space. If the non-inert materials need to be stored on site for a short period, the materials shall be centralized and stored at specific areas far away the sensitive receivers.	✓			
•	All Public Fill arising from the demolition works shall be limited to a size not more than 250mm and free of reinforcement bars, timber, etc. before re-using it.	✓			
•	Recyclable materials sorted from the site should be collected by potential recycling contractors under the Contractor's arrangement.	✓			
•	Trip ticket system will be implemented to ensure proper waste disposal at public filling and landfills	✓			
•	Appropriate measures should be employed to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	✓			
•	Proper resource planning and calculations before ordering the construction materials to be used will ensure that the wastage of the materials can be minimized	✓			



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
• Proper storage will minimize the damage and thus the wastage of the materials	/			
• Training of site personnel in proper waste management procedures. The workers shall be constantly educated for the awareness of the proper handling of waste and to reduce the amount of waste while Site Agent shall be constantly met to discuss the effectiveness of the implementation of the waste management plan. Information to promote the waste management and the reduction concept shall be posted at the site to raise alertness of the personnel concerned.	/			
• Chemical Waste				
• It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (General) Regulation should be observed and complied with for control of chemical wastes.	/			
• After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.		/		1 2
• Chemical wastes should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.	/			
• Containers used for the storage of chemical wastes				
• Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed	/			
• Have a capacity of less than 450L unless the specification have been approved by the EPD	/			
• Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Chemical Waste (General) Regulations and Codes of Practice	/			
• Labelling	/			
• Every container of chemical waste would bear an appropriate label, which would contain the particulars details.	/			
• The waste produced would ensure that the information contained on the label is accurate and sufficient so as to enable proper and safe handling, storage and transport of the chemical waste	/			
• Storage Area				
• Be clearly labeled and used solely for the storage of chemical waste	/			
• Be enclosed on at least 3 sides	/			
• Have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest	/			
• Have adequate ventilation	/			
• Be covered to prevent rainfall entering	/			
• Be arranged so that incompatible materials are adequately separated	/			
• Be clean and maintain regularly	/			
• Disposal				
• Be via a licensed waste collector	/			
• To a licensed disposal facility, such as Chemical Waste Treatment Centre	/			
• Be a reuser of the waste, under approval from the EPD	/			






SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
• Spillage				
• Establish source of spill or discharge and determine nature of material, where possible halt discharge				
• Commencing at the source of the spill, establish all current and potential impacted areas				
• Commence containment of spill using bunds made from available materials and ground water cut-off trenches where necessary				
• After spill is contained remove material (including contaminated soil where necessary) using pumps and/or absorbent materials				
• Dispose of materials as chemical wastes				
• General Refuse				
• General refuse generated on-site is in enclosed bins or compaction units separate from construction and chemical waste	/			
• A reputable waste collector is employed by the Contractor to remove general refuse from the site, separately from the construction and chemical waste.	/			
• General refuse generated is removed on daily or every second day basis to minimise odour, pest and litter impacts	/			
• Aluminium cans are recovered from the waste stream by individual collectors if they are segregated or easily accessible, so separate, labelled bins for their deposit should be provided if feasible.	/			
• Office wastes are reduced through recycling of paper if volumes are large enough to warrant collection.	/			
• Site Practice				
• Good site practices should be adopted to clean the rubbish and litter on the construction sites so as to prevent the rubbish and litter from dropping into the nearby environment. Construction sites should be cleaned on a regular basis.	/			
• The Contractor assigned worker is responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	/			
• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.	/			
• The Environmental Permit should be displaced conspicuously on site	/			
• Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	/			
• Any unused chemicals or those with remaining functional capacity should be recycled.	/			
• A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.	/			
• Suitable collection sites around site offices will be required. For environmental hygiene reasons and to minimize odor, refuse should not be stored for a period exceeding 48 hours, however, removal every 24 hours is preferable.	/			
• Minimize windblown litter and dust during transportation by either covering trucks or transporting wastes in enclosed container.	/			
• All generators, fuel and oil storage are within bundle areas.	/			
• Oil leakage from machinery, vehicle and plant is prevented.	/			
• Chemical storage area, drainage systems, silt traps, sumps and oil interceptors are cleaned and maintained regularly.	/			

Contract No.: TP 37/03 Remaining Engineering Infrastructure Works for Pak Shek Kok Development Package 2A

Table for follow-up Action:

Item	Details of defective works or observations	Location	Further action to be taken (Included persons / party to take action)	Expected Date for Action taken
1.	Follow up action to the previous site inspection item 2 on 14-3-2008, the pesticide was applied in drainage channel and temporary ditches at Void Abutment.	Void Abutment	Follow up action was completed, no further action to be taken.	N/A
2.	Follow up action to the previous site inspection item 3 on 15-3-2008, chemical oil was still noted on the ground without drip tray at Void Abutment.	Void Abutment	The contractor was reminded to provide drip tray for all chemical oil.	28-3-2008
			LWKJY	ET
Signature:				
Name:	Terry Lau		H.T. Cheung	
Date:	20/03/08	20/3/2008		20-3-2008

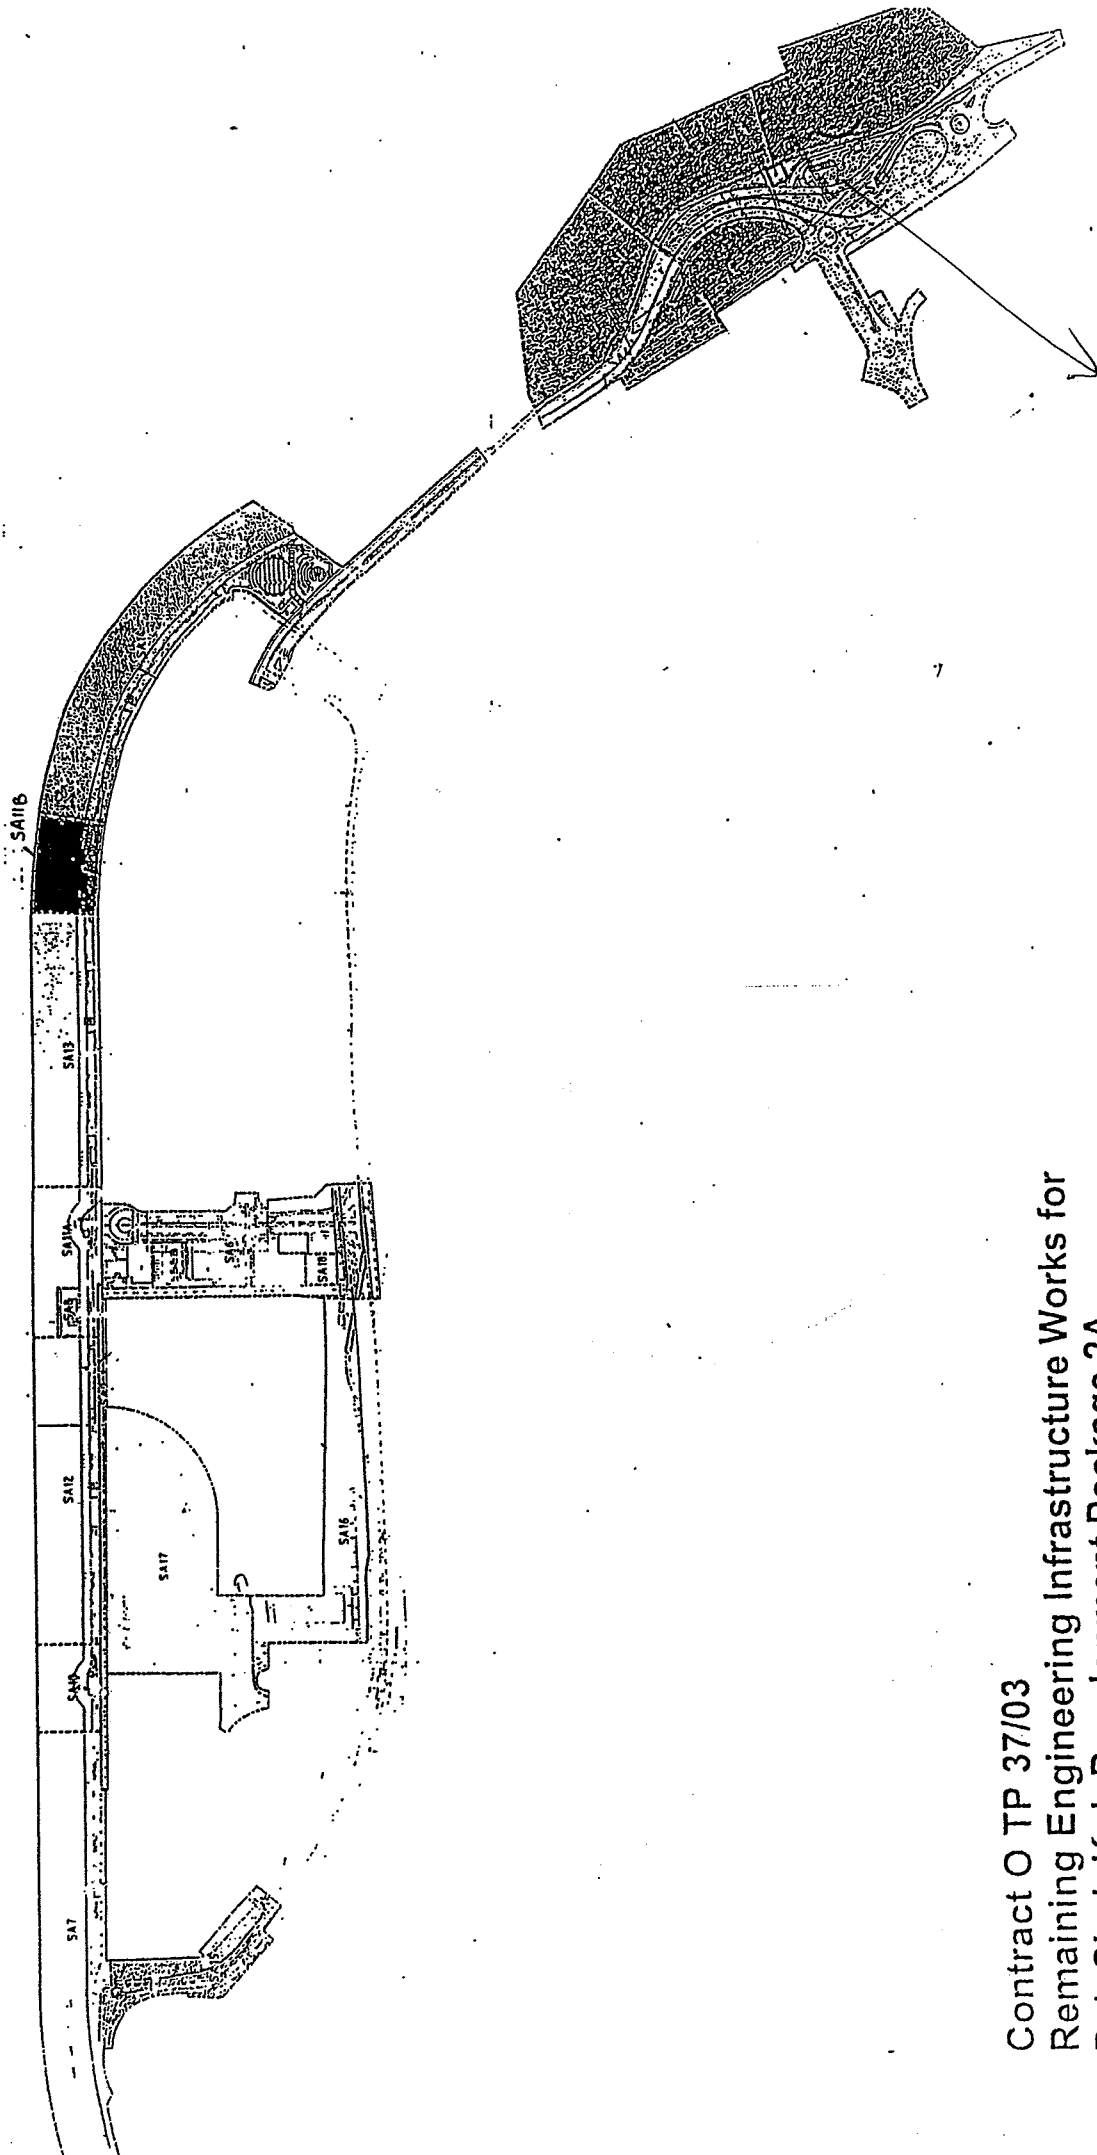

Item 2 (Used Abutment)

Contract O TP 37/03
 Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2A

Location and Key Plan

Contract No.: TP 37/03 Remaining Engineering Infrastructure Works for
Pak Shek Kok Development Package 2A

SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

Inspection Date : 28/3/8
 Time : 14:15
 Weather Condition : Sunny / Fine / Overcast / Drizzle / Rain / Storm / Hazy
 Wind : Calm / Light / Breeze / Strong
 Inspected by Name : (RSS) Michelle Fung.
 Signature : *[Signature]*
 (LWKJN) WATSON *[Signature]* (ET) Linda Lam
 Temperature : 23°C
 Humidity : High / Moderate / Low

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
Air Quality				
▪ The heights from which fill materials are dropped should be controlled to a practical height to minimize the fugitive dust arising from unloading.	<input checked="" type="checkbox"/>			
▪ During transportation by truck, material should be loaded to a level lower than the side and tail boards, and should be dampened or covered before transport.	<input checked="" type="checkbox"/>			
▪ All stockpile of aggregate or spoil should be enclosed or covered and water applied in dry or windy condition.	<input checked="" type="checkbox"/>			
▪ The haul road should be either paved or regular watering.	<input checked="" type="checkbox"/>			
▪ Unpaved areas should be watered regularly to avoid dust generation.	<input checked="" type="checkbox"/>			
▪ The public road around the site entrance should be kept clean and free from dust.	<input checked="" type="checkbox"/>			
▪ Vehicle speed should be limited to 20 km/hr.	<input checked="" type="checkbox"/>			
▪ Wheel washing facilities should be provided at all main entrance of work site.	<input checked="" type="checkbox"/>			
▪ The enclosures should be around the main dust-generating activities.	<input checked="" type="checkbox"/>			
▪ Dusty materials should be sprayed prior to loading.	<input checked="" type="checkbox"/>			
▪ All plant and equipment should be well maintained e.g. without black smoke emission.	<input checked="" type="checkbox"/>			
▪ Vehicle and equipment should be switched off while not in use.	<input checked="" type="checkbox"/>			
▪ Open burning should be prohibited.	<input checked="" type="checkbox"/>			
Noise				
▪ The constructions works should be scheduled to minimize noise nuisance.	<input checked="" type="checkbox"/>			
▪ Only well maintained plant should be operated on-site and plant should be serviced regularly during the construction works.	<input checked="" type="checkbox"/>			
▪ Machines and plants that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.	<input checked="" type="checkbox"/>			
▪ Plant known to emit noise strongly in on direction, should, where possible, be covered or shielded by appropriate acoustic materials.	<input checked="" type="checkbox"/>			
▪ Powered mechanical equipment (PME) should be covered or shielded by appropriate acoustic materials.	<input checked="" type="checkbox"/>			
▪ Noise enclosures, noise barriers, or portable noise barriers used where necessary.	<input checked="" type="checkbox"/>			
▪ Air compressors and hand held breakers should have noise labels.	<input checked="" type="checkbox"/>			
▪ Compressors and generators should operate with door closed.	<input checked="" type="checkbox"/>			
▪ Construction Noise Permits should be available for inspection.	<input checked="" type="checkbox"/>			



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

Mitigation Measures on Waste Management	Implementation Stages*			Remark
	Yes	No	N/A	
	/	/	/	
Water Quality				
General Construction Activities				
• Temporary ditches shall be provided to facilitate runoff discharge into appropriate watercourses, via a sediment trap / sedimentation tanks, prior to discharge.	/			
• Permanent drainage channels shall incorporate sediment basins / traps, and baffles.	/			
• All traps shall incorporate oil and grease removal facilities.	/			
• Sediment traps / sedimentation tanks shall be regular cleaned and maintained regularly.	/			
• All drainage facilities should be adequate for controlled release of storm flows.	/			
• Minimizing of exposed soil areas to reduce the potential for increased siltation and contamination of runoff.	/			
• Open stockpiles of more than 50m ² should be covered.	/			
• Temporary stockpiles of excavated materials should be covered during rainstorms.	/			
• Manholes should be covered and sealed.	/			
• All chemical stores shall be contained (bunded) such that spills are not allowed to gain access to water bodies.	/			
• Vehicles and plant should be cleaned of earth, mud and debris before leaving the site.	/			
• Vehicle washing facilities should be provided at every site exit.	/			
• Vehicle washing facilities should be adequate to settle out the sand and silt.	/			
• Washing area and road exiting from washing facility should be paved.	/			
• Access road should have sufficient back fall toward washing facility.	/			
Dredging Activities				
• Dredging of designated contaminated marine mud shall only be undertaken by a suitable grab dredger using a close grab.	/			
• Mechanical grabs shall be designed and maintained to avoid spillage and shall be seal tightly while being lifted.	/			
• All vessels shall be sized such that adequate clearance is maintained between vessel and the sea bed and under water pipelines at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller on the water within the site.	/			
• The works shall cause no visible foam, oil, grease, scum litter or other objectionable matter to be present on the water within the site.	/			
• All barges shall be fitted with tight fitting seals to their bottom openings to prevent leakage of materials.	/			
• Excess material shall be cleaned from the decks and exposed fittings of the barges before the vessels are moved.	/			
• Loading of barges shall be controlled to prevent splashing of dredging material to the surrounding water and the barges shall not be filled to a level which will cause overflowing of material or polluted water during loading or transportation.	/			
• Adequate freeboard shall be maintained on barges to ensure that decks are not washed by wave action.	/			



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*			Remark
	Yes	No	N/A	
Mitigation Measures on Waste Management				
Filling Activities				
▪ Use of silt screen around the filling face to reduce the losses to the surrounding.			✓	
▪ All vessels shall be sized such that adequate clearance is maintained between vessel and the sea bed and under water pipeline at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash or pipelines damaged.			✓	
▪ The works shall cause no visible foam, oil, grease, scum, litter or other objectionable matter to be present on the water within the site.			✓	
▪ All barges shall be fitted with tight fitting seals to their bottom openings to prevent leakage of material.			✓	
▪ Loading of barges shall be controlled to prevent splashing of dredged material to the surrounding water and barges shall not be filled to a level which will cause overflowing of material or polluted water during loading transportation.			✓	
Waste Management				
Marine Dredged Sediment				
• Relevant licence / permits for disposal of marine dredged sediment are available for inspection.			✓	
• Bottom opening of barges is fitted with tight fitting seals to prevent leakage of material. Excess material is cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.			✓	
• Monitoring of the barging loading is conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels are equipped with automatic self-monitoring devices as specified by the EPD.			✓	
• Transport of dredged marine sediments to the disposal site is by split barge of not less than 750m ³ capacity, well maintained and capable of rapid opening and discharge at the disposal site.			✓	
• Inspection of the barge loading to ensure that loss of material does not take place during transportation.			✓	
Construction and Demolition (C&D) Waste				
• Most of the C&D materials generated from the construction are sorted immediately in-situ to find out if they can be re-used for this job site or for other job sites.	✓			
• Sufficient spaces are identified and provided during the construction stage for the collection, temporary storage and on-site sorting of C&D materials.	✓			
• Proper protective measures, such as fences and tarpaulin, are provided, in order to protect the temporary stockpiled materials for later reuse / recycle.	✓			
• Avoiding cross contamination to reusable and / or recyclable materials collected (e.g. covering the reusable materials)	✓			
• In order to reduce the impacts to the public, except for those sorted inert C&D materials to be reused on site, all other sorted non-inert materials (e.g. general refuse and waste formworks) shall be removed off site as soon as practicable in order to optimise the use of the on-site storage space. If the non-inert materials need to be stored on site for a short period, the materials shall be centralized and stored at specific areas far away the sensitive receivers.	✓			
• All Public Fill arising from the demolition works shall be limited to a size not more than 250mm and free of reinforcement bars, timber, etc. before re-using it.	✓			
• Recyclable materials sorted from the site should be collected by potential recycling contractors under the Contractor's arrangement.	✓			
• Trip ticket system will be implemented to ensure proper waste disposal at public filling and landfills	✓			
• Appropriate measures should be employed to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.	✓			
• Proper resource planning and calculations before ordering the construction materials to be used will ensure that the wastage of the materials can be minimized	✓			



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*		Remark
	Yes	No / N/A	
Mitigation Measures on Waste Management			
• Proper storage will minimize the damage and thus the wastage of the materials	/		
• Training of site personnel in proper waste management procedures. The workers shall be constantly educated for the awareness of the proper handling of waste and to reduce the amount of waste while Site Agent shall be constantly met to discuss the effectiveness of the implementation of the waste management plan. Information to promote the waste management and the reduction concept shall be posted at the site to raise alertness of the personnel concerned.	/		
• Chemical Waste			
• It is required to register as a chemical waste producer if chemical wastes would be produced from the construction activities. The Waste Disposal Ordinance (Cap 354) and its subsidiary regulations in particular the Waste Disposal (Chemical Waste) (General) Regulation should be observed and complied with for control of chemical wastes.	/		
• After use, chemical wastes (e.g. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.	/		
• Chemical wastes should be stored and collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licensed facility in accordance with the Chemical Waste (General) Regulation.	/		
• Containers used for the storage of chemical wastes			
• Be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed	/		
• Have a capacity of less than 450L unless the specification have been approved by the EPD	/		
• Display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Chemical Waste (General) Regulations and Codes of Practice	/		
• Labelling			
• Every container of chemical waste would bear an appropriate label, which would contain the particulars details.	/		
• The waste produced would ensure that the information contained on the label is accurate and sufficient so as to enable proper and safe handling, storage and transport of the chemical waste	/		
• Storage Area			
• Be clearly labeled and used solely for the storage of chemical waste	/		
• Be enclosed on at least 3 sides	/		
• Have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20% of the total volume of waste stored in that area, whichever is the greatest	/		
• Have adequate ventilation	/		
• Be covered to prevent rainfall entering	/		
• Be arranged so that incompatible materials are adequately separated	/		
• Be clean and maintain regularly	/		
• Disposal			
• Be via a licensed waste collector	/		
• To a licensed disposal facility, such as Chemical Waste Treatment Centre	/		
• Be a reuser of the waste, under approval from the EPD	/		



SITE INSPECTION CHECKLIST ON THE IMPLEMENTATION OF ENVIRONMENTAL MITIGATION MEASURES

	Implementation Stages*	Remark
Mitigation Measures on Waste Management		
• Spillage		
• Establish source of spill or discharge and determine nature of material, where possible halt discharge	/	
• Commencing at the source of the spill, establish all current and potential impacted areas	/	
• Commence containment of spill using bunds made from available materials and ground water cut-off trenches where necessary	/	
• After spill is contained remove material (including contaminated soil where necessary) using pumps and/or absorbent materials	/	
• Dispose of materials as chemical wastes	/	
• General Refuse		
• General refuse generated on-site is in enclosed bins or compaction units separate from construction and chemical waste	/	
• A reputable waste collector is employed by the Contractor to remove general refuse from the site, separately from the construction and chemical waste.	/	
• General refuse generated is removed on daily or every second day basis to minimise odour, pest and litter impacts	/	
• Aluminium cans are recovered from the waste stream by individual collectors if they are segregated or easily accessible, so separate, labelled bins for their deposit should be provided if feasible.	/	
• Office wastes are reduced through recycling of paper if volumes are large enough to warrant collection.	/	
• Site Practice		
• Good site practices should be adopted to clean the rubbish and litter on the construction sites so as to prevent the rubbish and litter from dropping into the nearby environment. Construction sites should be cleaned on a regular basis.	/	
• The Contractor assigned worker is responsible for good site practices, arrangements for collection and effective disposal to an appropriate facility, of all wastes generated at the site.	/	
• Proper storage and site practices to minimise the potential for damage or contamination of construction materials.	/	
• The Environmental Permit should be displaced conspicuously on site	/	
• Plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.	/	
• Any unused chemicals or those with remaining functional capacity should be recycled.	/	
• A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be used, e.g. trip ticket system for chemical waste disposal. Quantities could be determined by weighing each load or other suitable methods.	/	
• Suitable collection sites around site offices will be required. For environmental hygiene reasons and to minimize odor, refuse should not be stored for a period exceeding 48 hours, however, removal every 24 hours is preferable.	/	
• Minimize windblown litter and dust during transportation by either covering trucks or transporting wastes in enclosed container.	/	
• All generators, fuel and oil storage are within bundle areas.	/	
• Oil leakage from machinery, vehicle and plant is prevented.	/	
• Chemical storage area, drainage systems, silt traps, sumps and oil interceptors are cleaned and maintained regularly.	/	

Table for follow-up Action:

Item	Details of defective works or observations	Location	Further action to be taken (Included persons / party to take action)	Expected Date for Action taken
1.	Follow up action to the previous site inspection item 3 on 15/3/18 and item 2 on 20/3/18, no chemical containers were noted at void Abutment	Void Abutment	Since the observation was improved, no further action should be taken.	N/A
	No new observations were noted in this weekly site inspection.			

Signature:	RSS	LWKJV	ET
Name:	Fung Fie Fie Michelle.	WALTON CHEN	Linda Lam
Date:	28 March 2018.	28 MARCH 2018	Linda Lam 28/3/18

Appendix I
IEC and RE Comments on Monthly EM&A Report
—
February 2008


IEC and RE Comments on Monthly Environmental Monitoring and Audit Report – February 2008

Item No.	Document Reference	Comment	ET Response
---	---	---	---



Figures

Updated Noise Monitoring Locations	Description
NM1	HKTB Staff Accommodation (on ground floor near the entrance facing south-east)
NM2	CUFHK Residence No.10
NM3	Cheung Shue Tan Village (near the outer building, temple)
NM4 – cancelled	Tsui Hong Village
NM5 – cancelled	Deerhill Bay Development
NM6 – cancelled	Educational Uses in Area 12 (Part I)
NM7 – cancelled	Residential Development (Low Rise Building) – R1

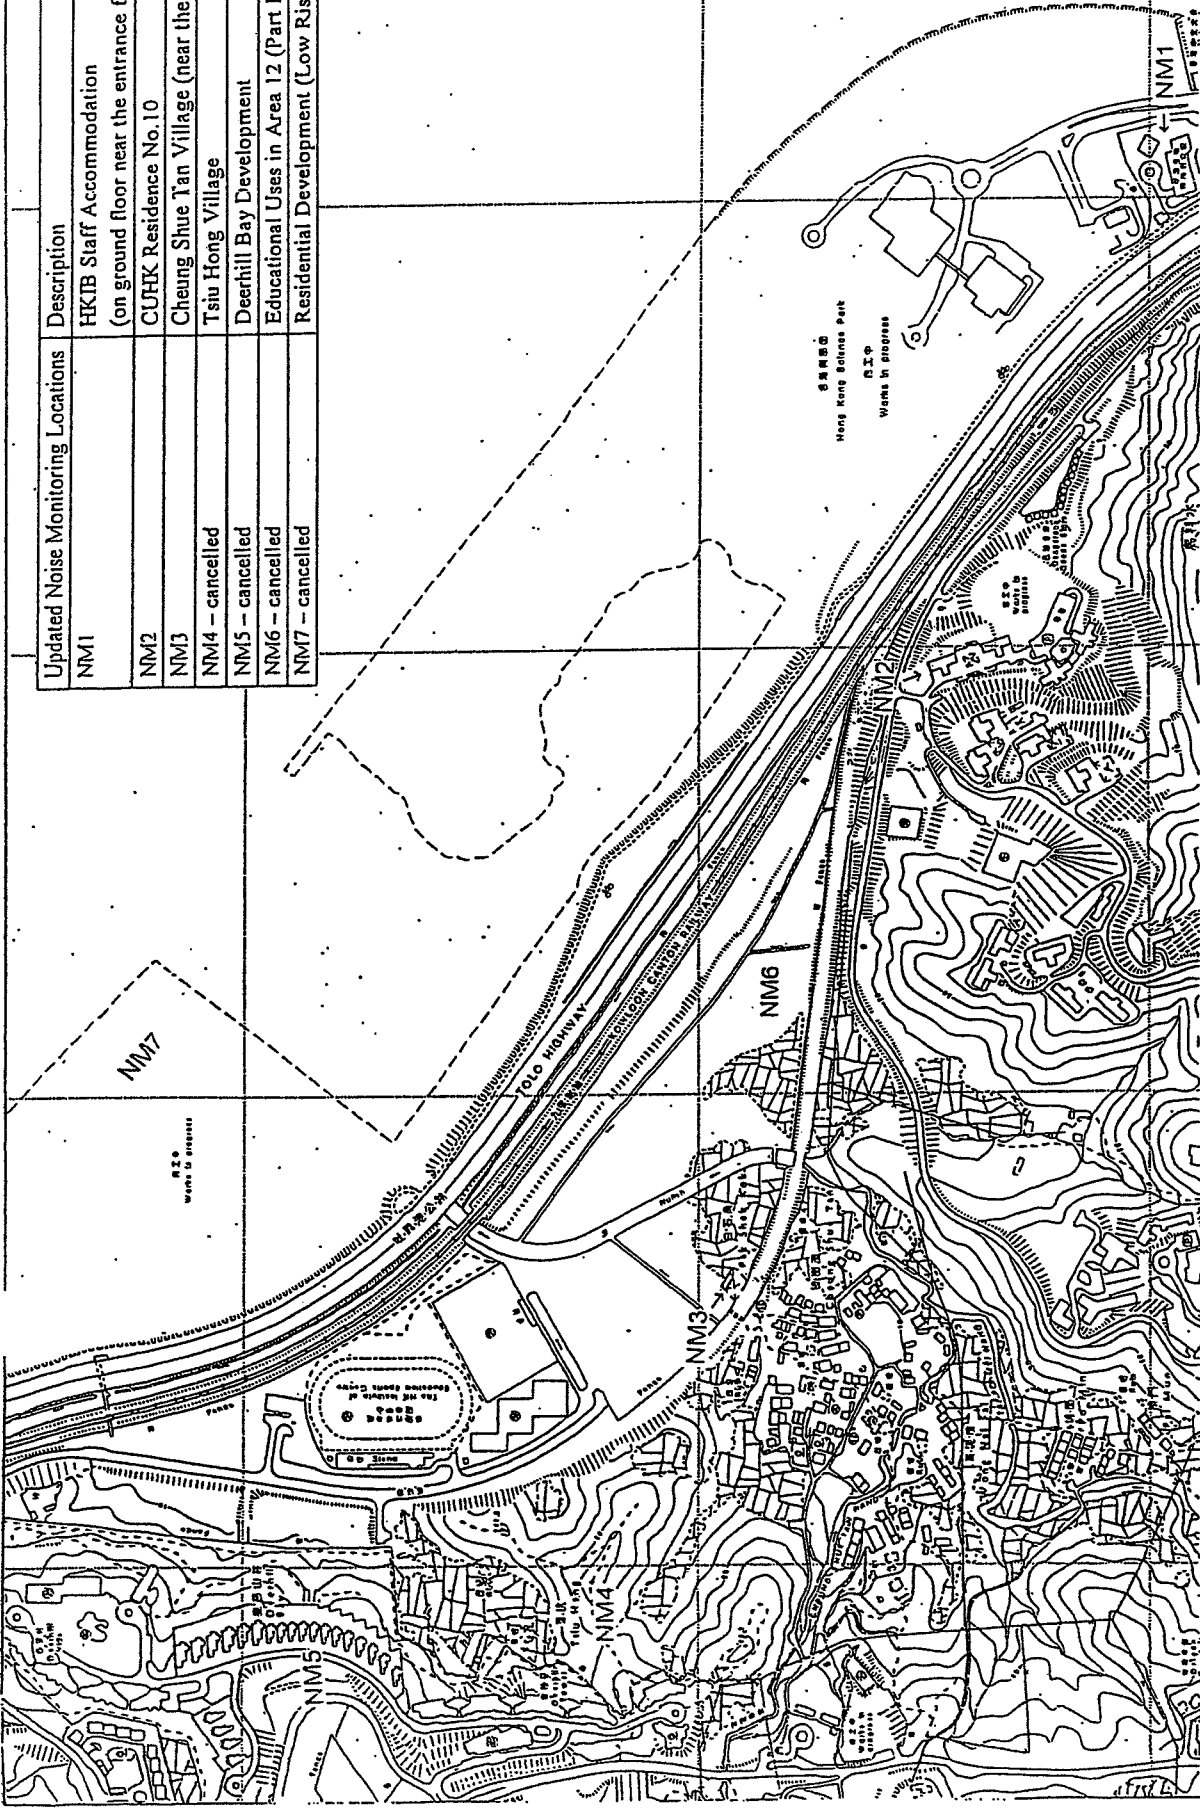


Scale : ---

Revised Date: June 2004

Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2A
 Contract No. TP 37/03
 Figure 1 Location of Noise Monitoring Stations



東業德勤測試顧問有限公司
 ETS-TESTCONSULT LIMITED

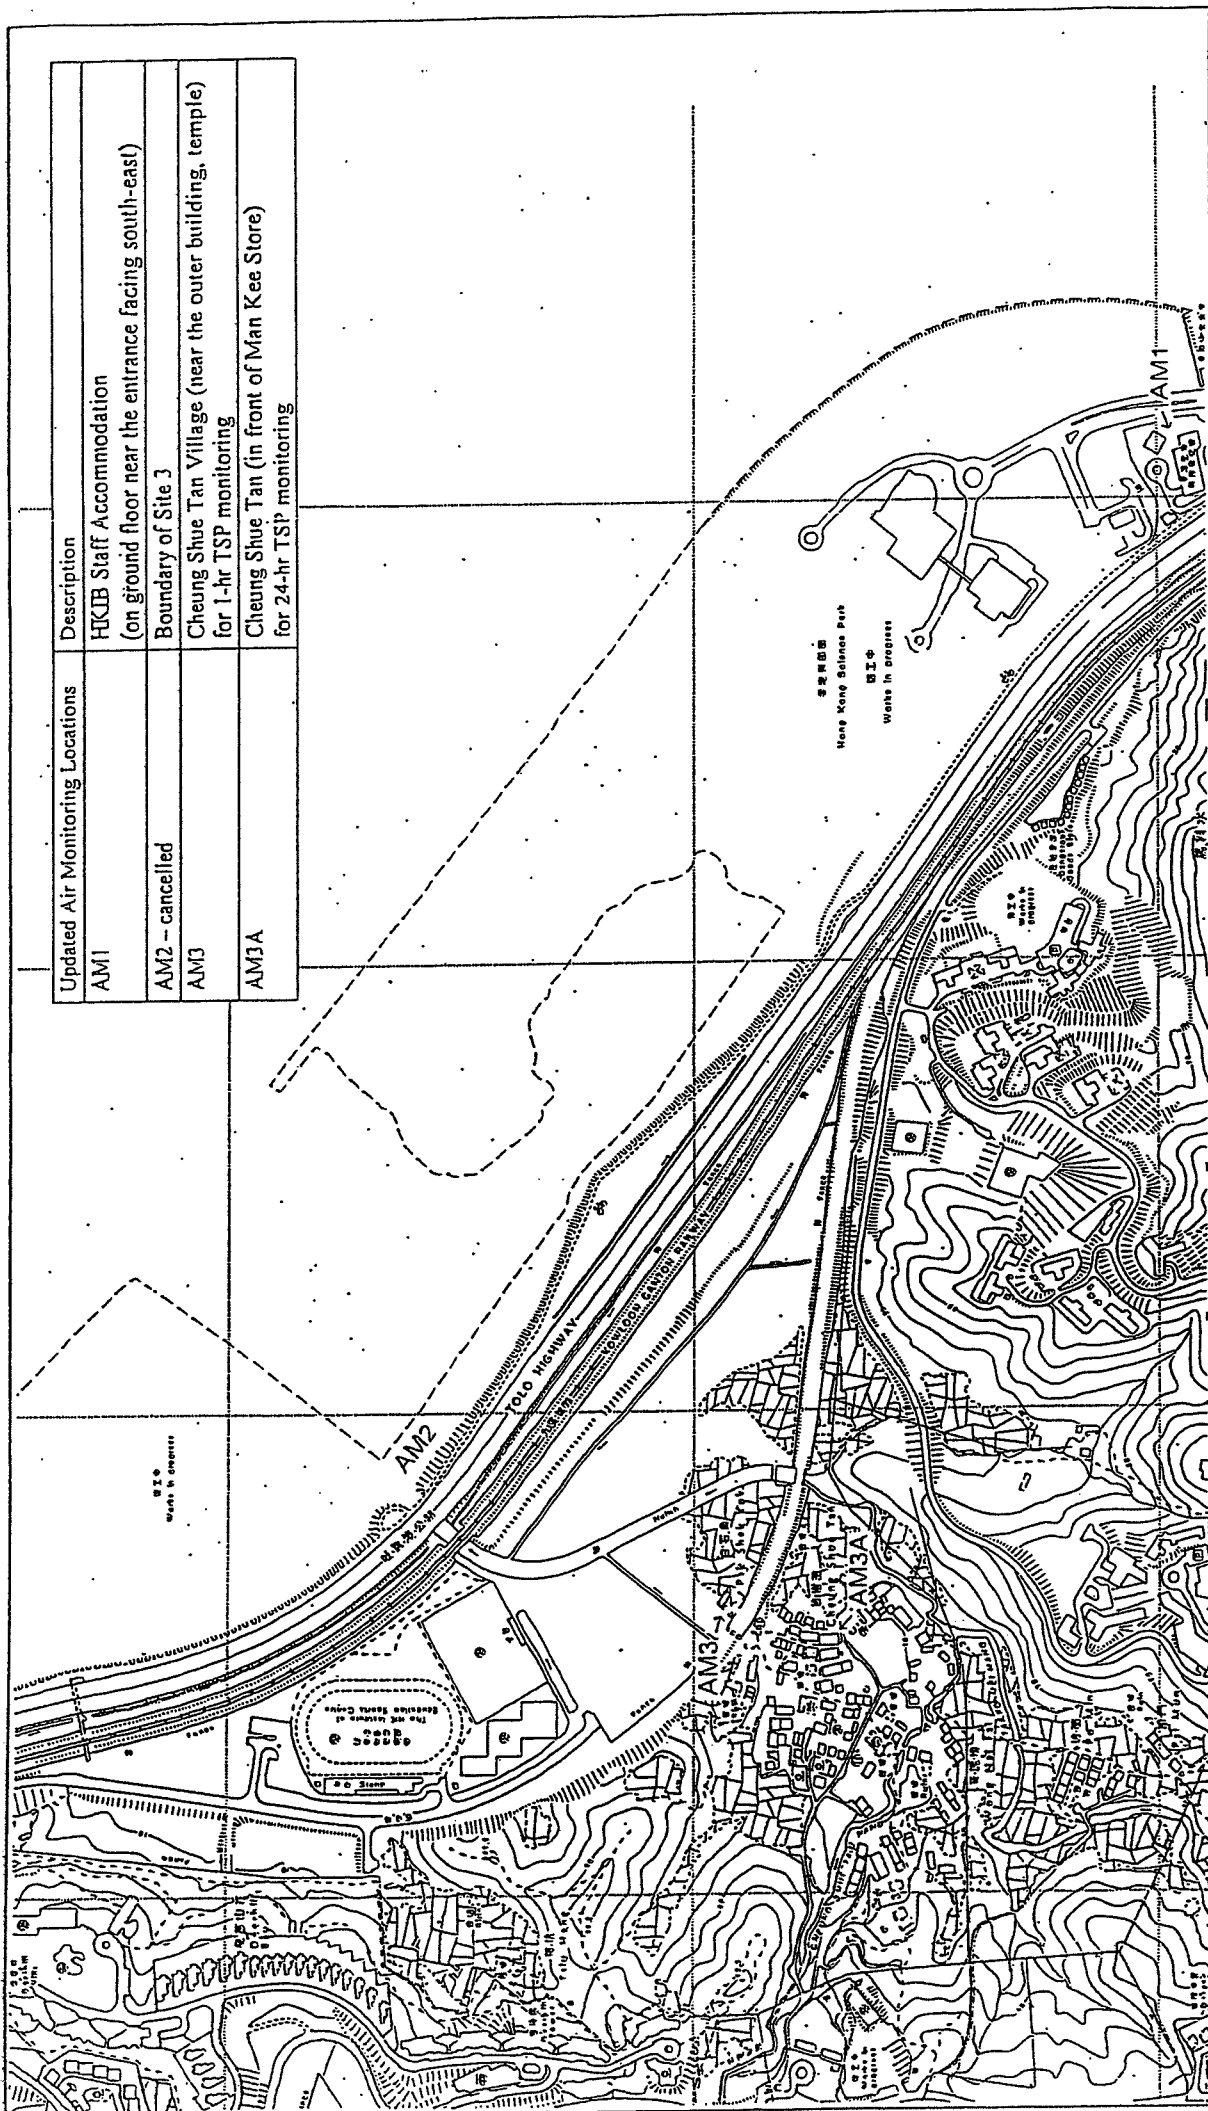


Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2 A
 Contract No. TP 37/03
 Figure 2 Location of Air Monitoring Stations

Scale : ---
 Revised Date: June 2004



專業德勤測試顧問有限公司
 ETS-TESTCONSULT LIMITED

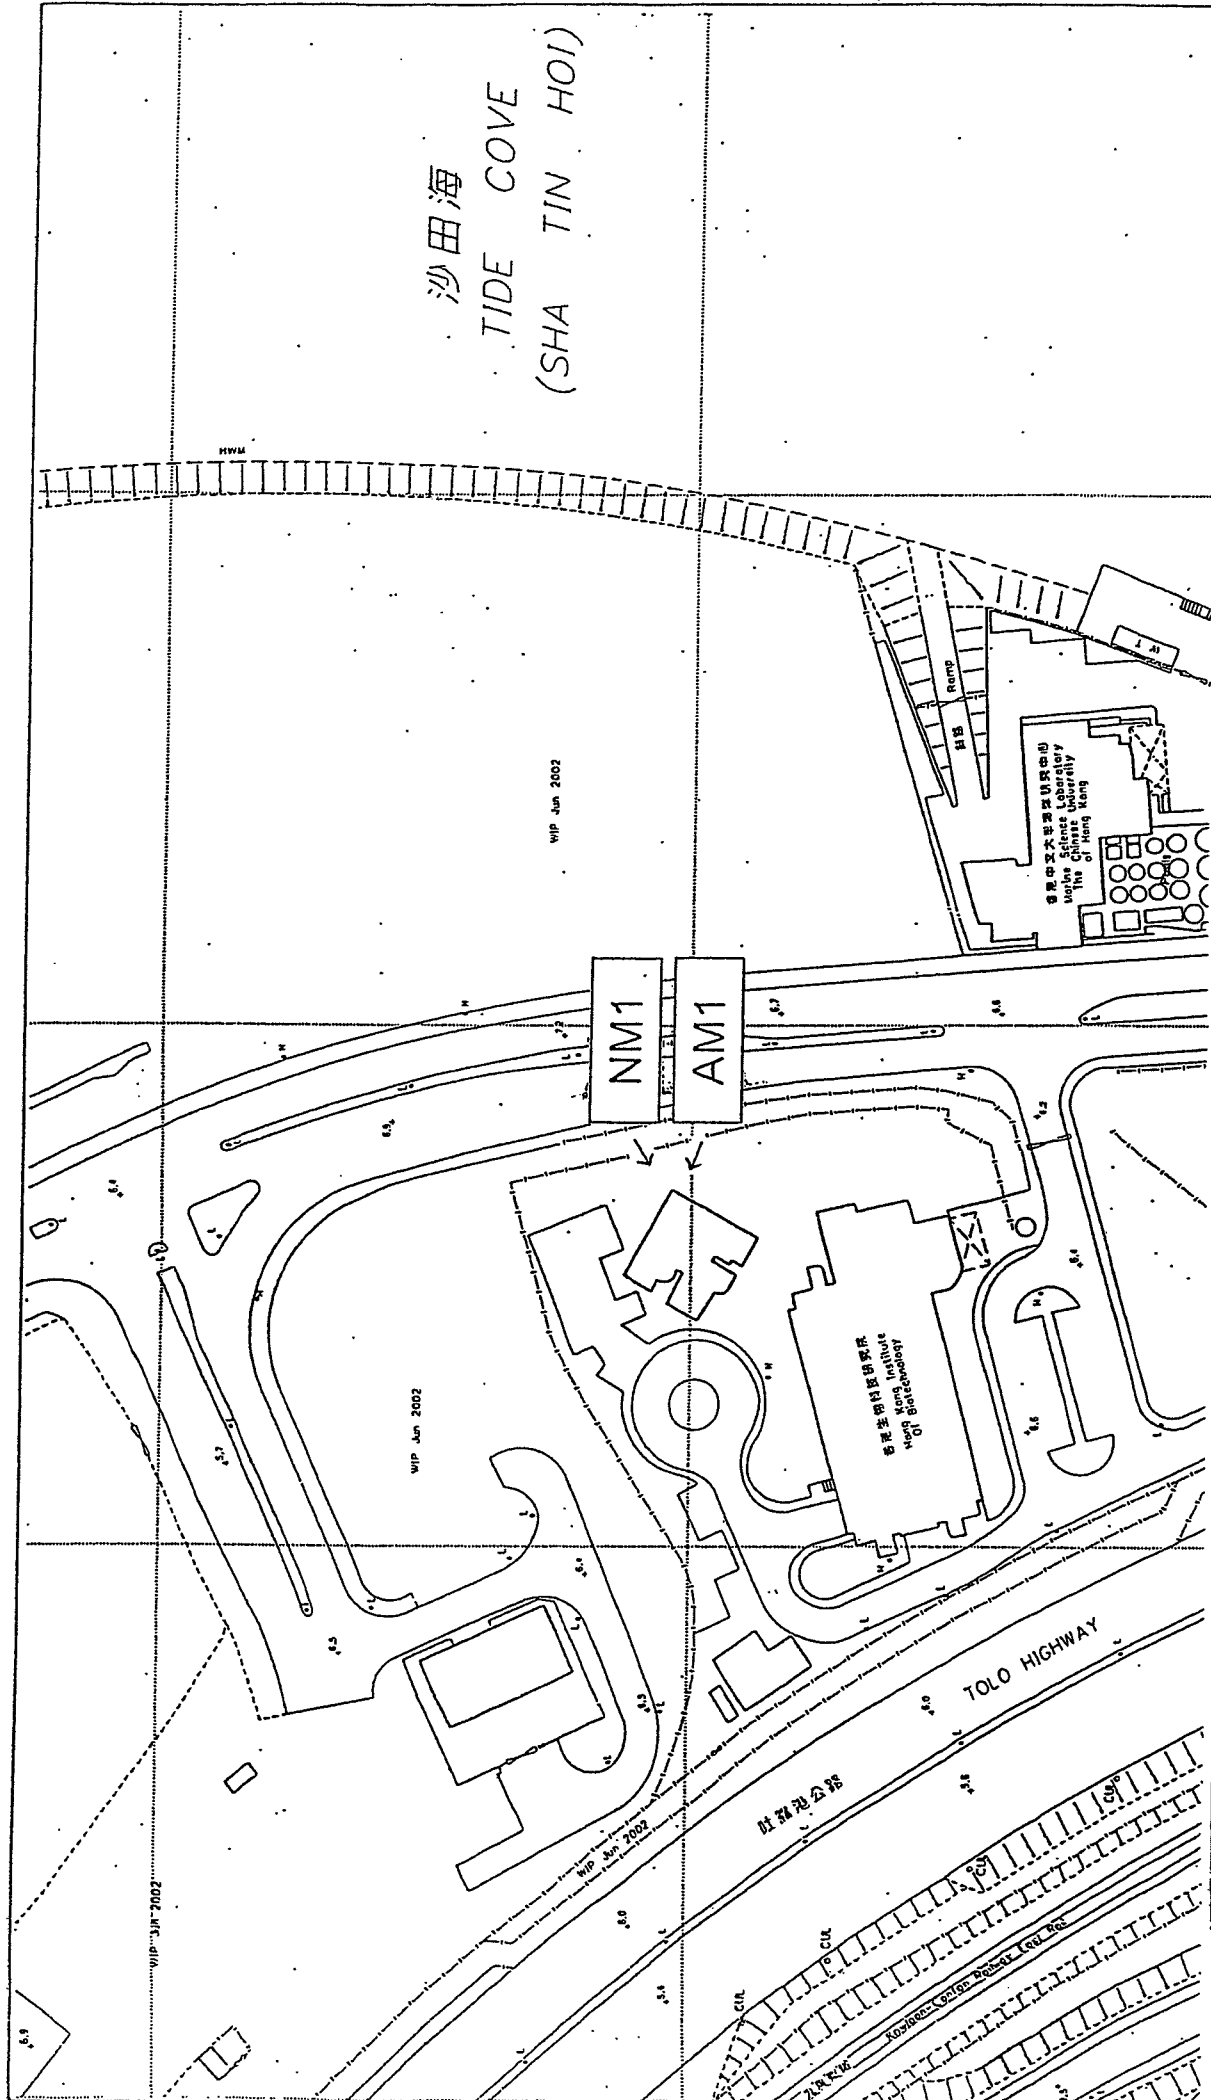

沙田海
TIDE COVE
(SHA TIN HOI)

Remaining Engineering Infrastructure Works for
Pak Shek Kok Development Package 2A
Contract No. TP 37/03
Figure 3 Location of Air and Noise Monitoring Stations
at HKIB Staff Accommodation

Scale : ---

Revised Date:

June 2004



專業檢測顧問有限公司
ETS-TESTCONSULT LIMITED




Scale : ---

Revised Date: June 2004



Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2 A
 Contract No. TP 37/03
 Figure 4 Location of Noise Monitoring Station at CUHK Residence No.10

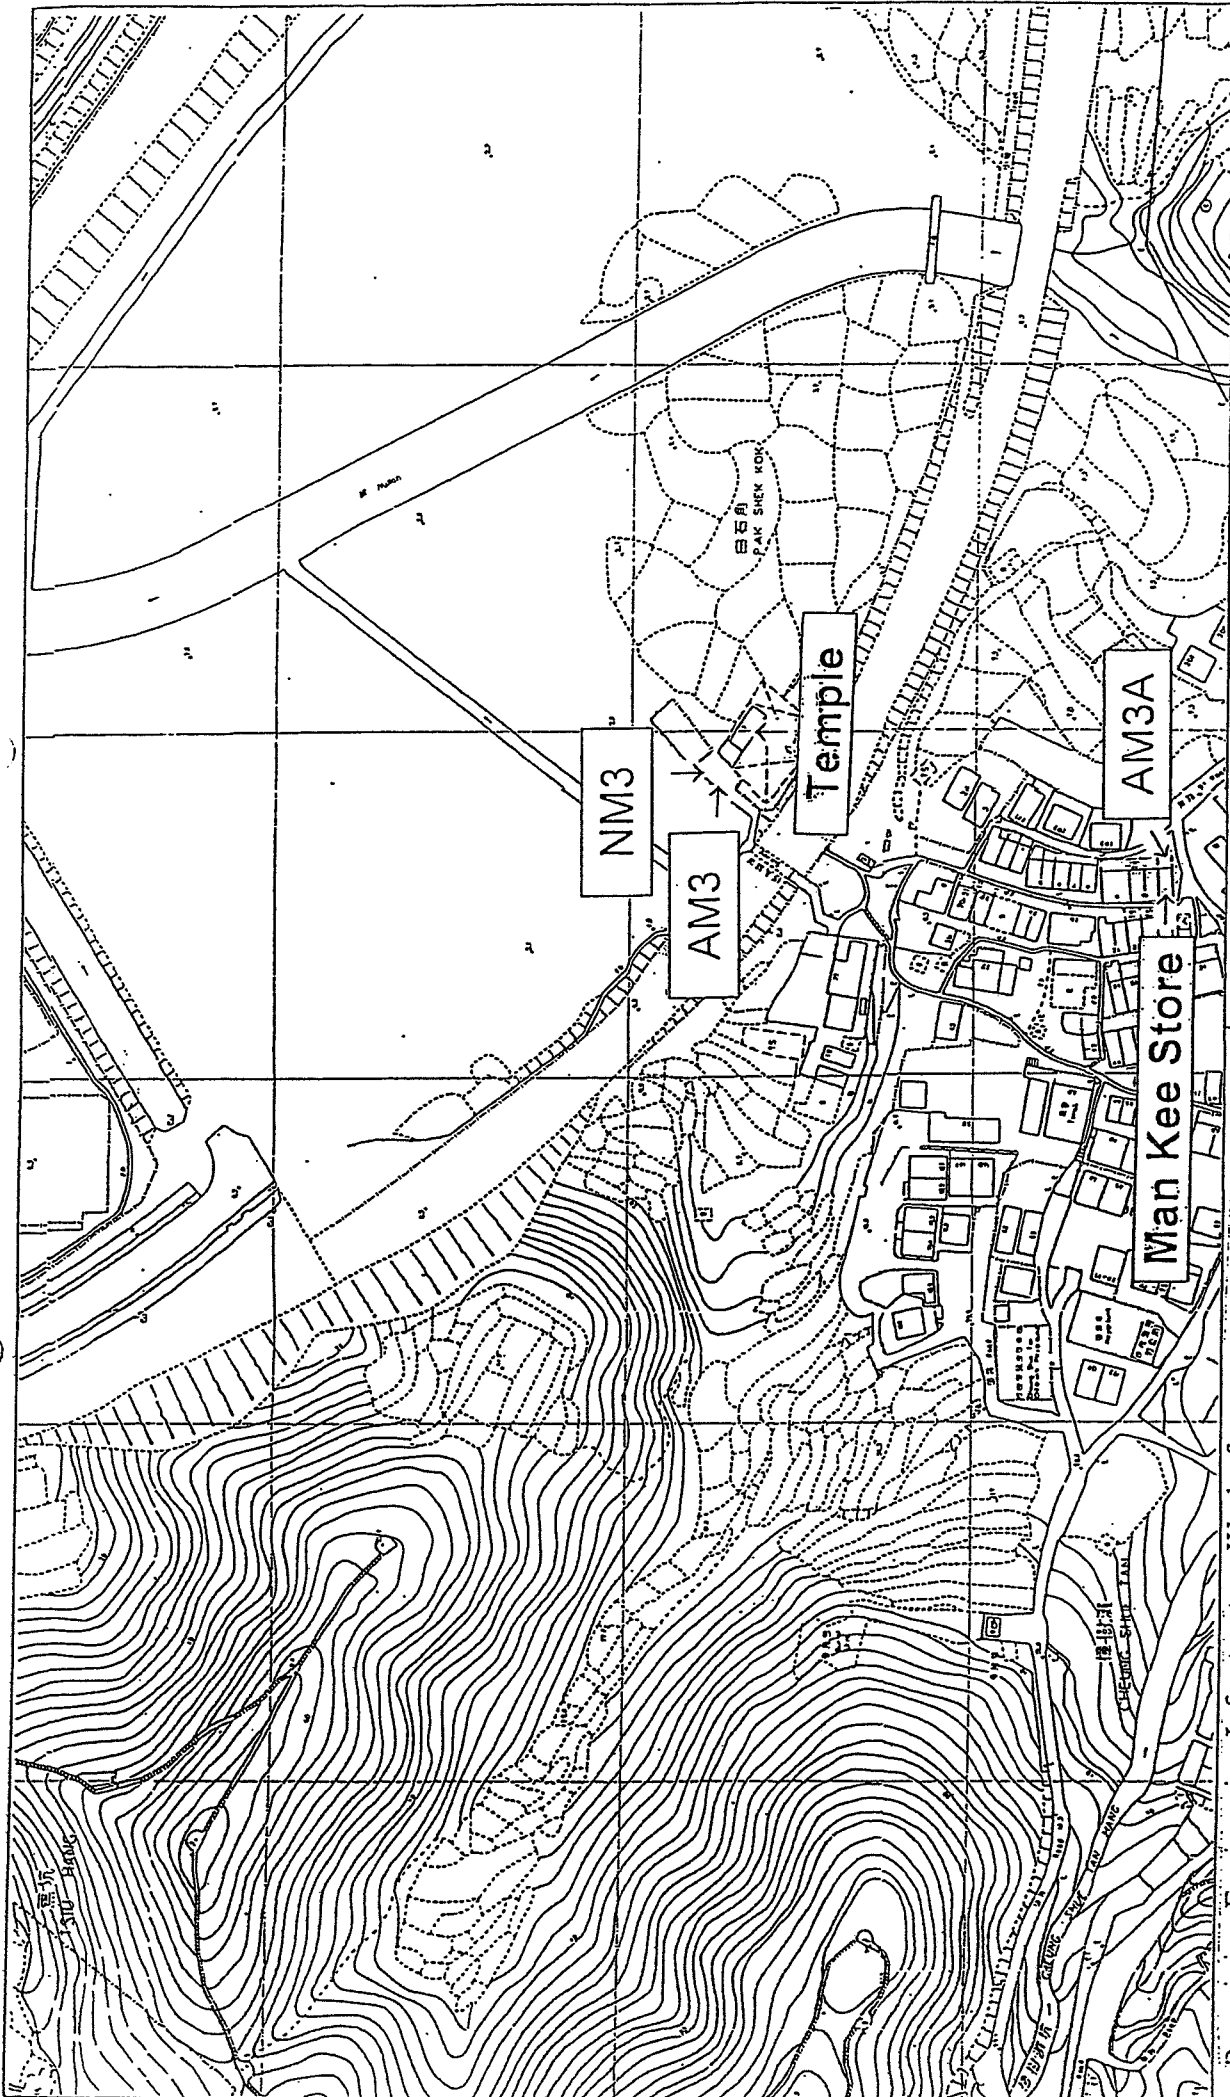

Remaining Engineering Infrastructure Works for
 Pak Shek Kok Development Package 2 A
 Contract No. TP 37/03
 Figure 5 Location of Air and Noise Monitoring Stations
 at Cheung Shue Tan Village


Scale : ---

Revised Date:

June 2004



東業德勤測試顧問有限公司
 ETS-TESTCONSULT LIMITED

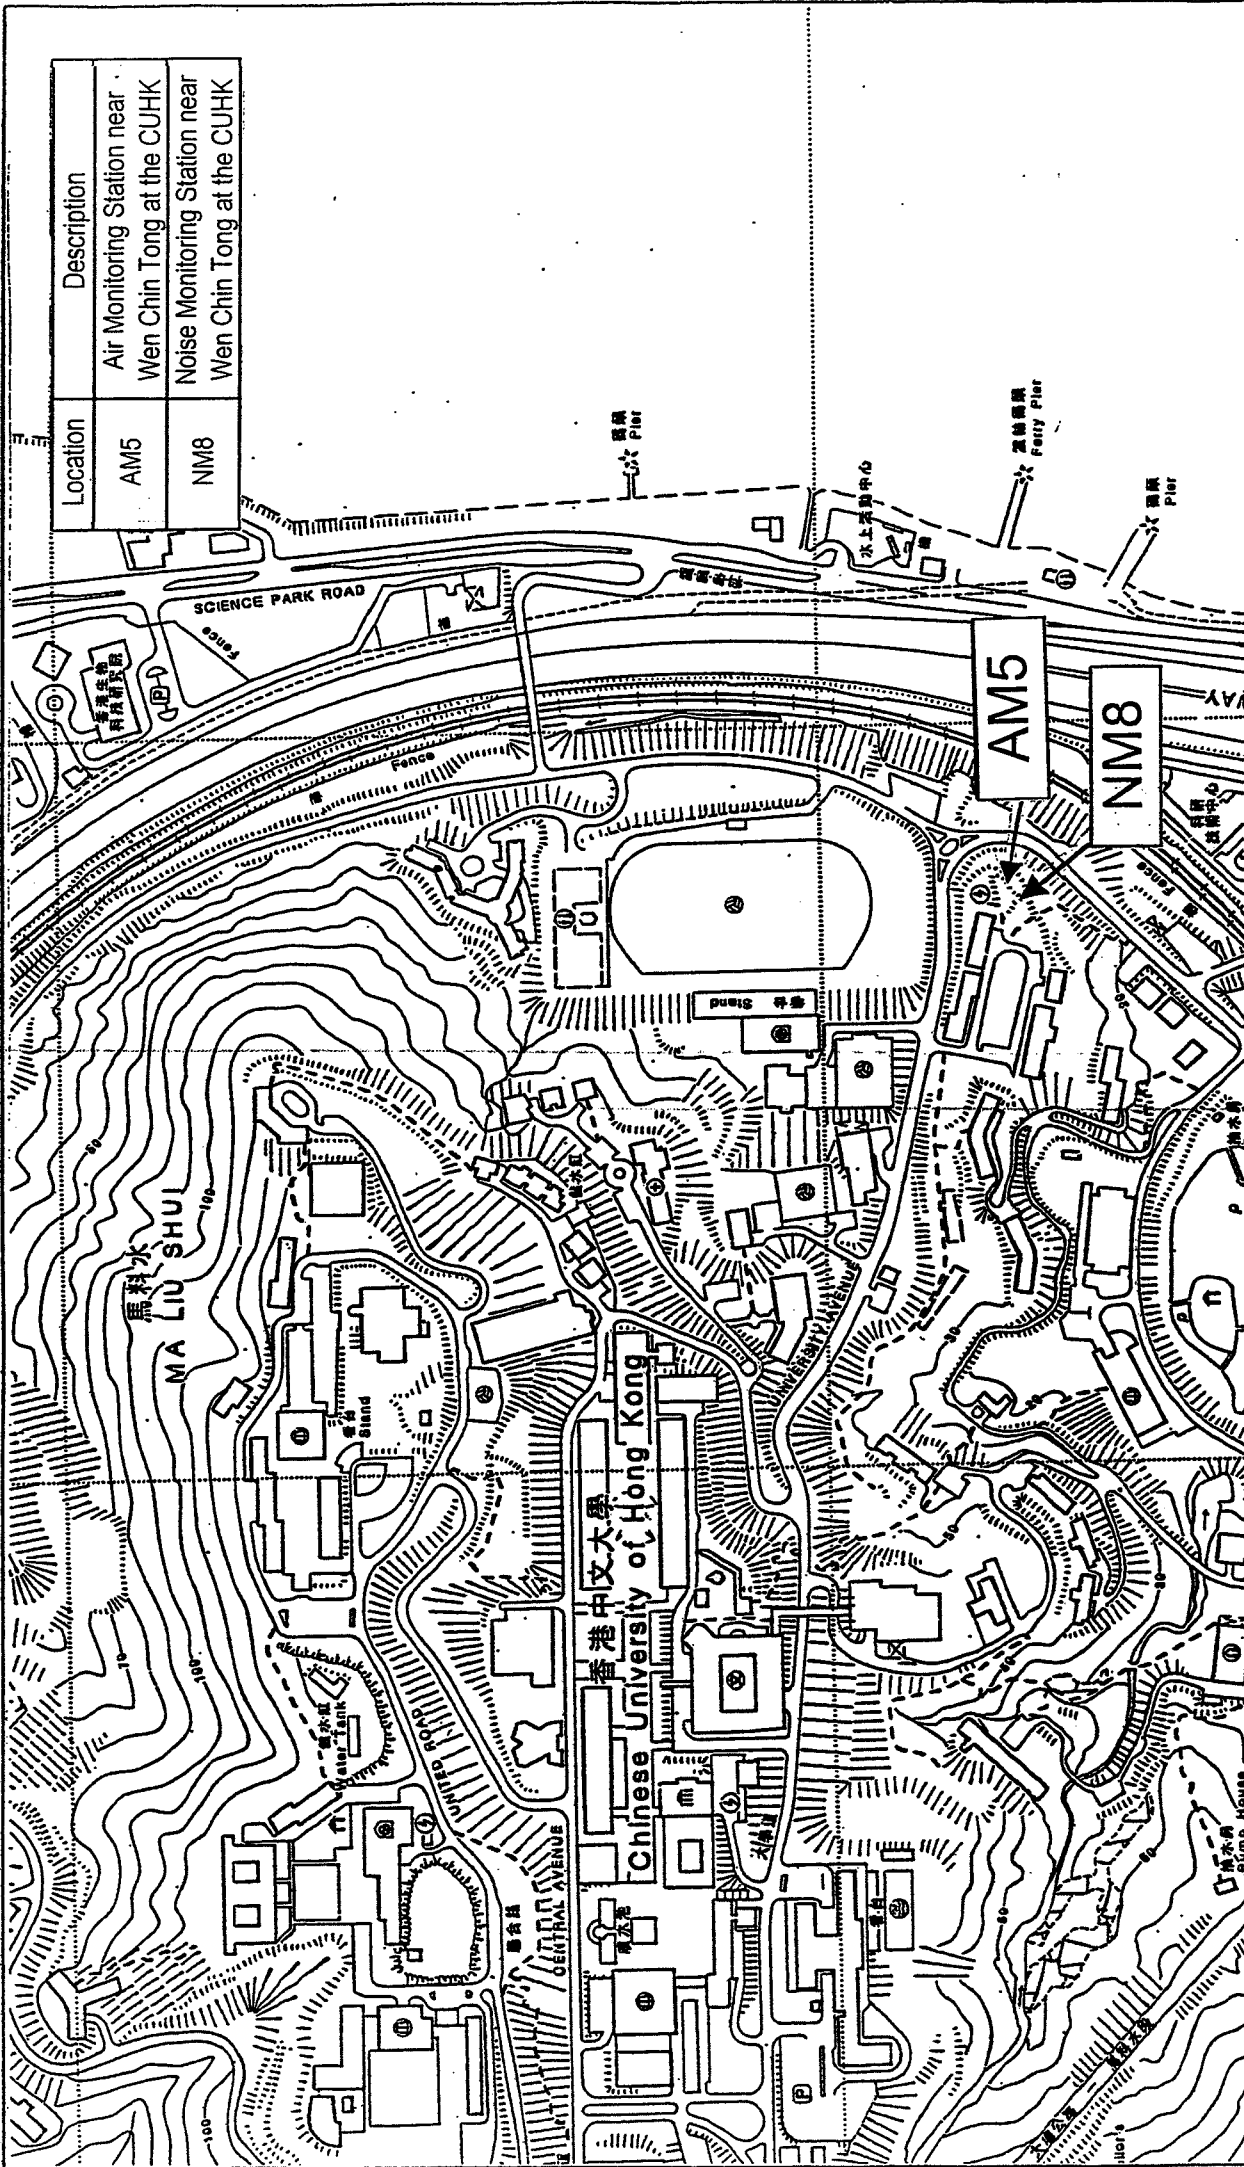

Remaining Engineering Infrastructure Works for Pak Shek Kok Development Scale : ---

Package 2A Contract No. TP 37/03

Figure 7 Additional Locations of Air and Noise Monitoring Stations at the Chinese University of Hong Kong

Revised Date :
October 2004



東業德動測試顧問有限公司
ETS-TESTCONSULT LIMITED
