FUGRO TECHNICAL SERVICES LIMITED

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233 Fax : +852-2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk

MateriaLab

Drainage Services Department, Contract No. DC/2006/01 Drainage Improvement Works in Sai Kung

Environmental Monitoring and Audit Report For November 2009

Client: Sum Kee Construction Limited

MateriaLab Ref. No. : 075117EN90615

Prepared by . ih Sze Checked by John Ho

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

GEN01/1208

CONTENTS

- 1. Executive Summary
- 2. Introduction
- 3. General Review
- 4. Construction Phase Environmental Monitoring
- 5. <u>Construction Site Environmental Audit</u>
- 6. Summary of Complaints, Summons and Successful Prosecutions
- 7. Works Programme for December 2009
- 8. Monitoring Schedule for December 2009
- 9. Comments and Conclusions for November 2009

APPENDICES

Appendix 1	Environmental Mitigation Measures
Appendix 2	Waste Management Guideline
Appendix 3	Environmental Mitigation Measures Implementation Schedule
Appendix 4	Data for Water and Noise Monitoring
Appendix 5	Graphical Presentation of Water and Noise Monitoring Data
Appendix 6	Event Action Plan for Air, Noise and Water Monitoring
Appendix 7	Equipment Details
Appendix 8	Figures
Appendix 9	Work Program

TABLES

Table 3.1	Summary of Monitored Parameters
Table 3.2	Action and Limit Level for Air Quality
Table 3.3	Action and Limit Level for Construction Noise
Table 3.4	Action and Limit Level for Water Quality
Table 4.1	Environmental Monitoring Schedule for this Reviewed Month
Table 4.2	Air Quality Monitoring Stations
Table 4.3	Noise Level Monitoring Stations
Table 4.4	Summary of Non-compliance for Water Quality
Table 8.1	Environmental Monitoring Schedule for the Forthcoming Month

FIGURES

Figure 1.1	Location of Project Site
Figure 3.2	Project Organization Structure
Figure 3.3	Organization Chart of Site Environmental Team
Figures (2.2,	Location of Environmental Air, Noise and Water Monitoring Stations
3.2 & 4.1-4.3)	

1. Executive Summary

The requisite construction works for the Drainage Services Department Contract No. DC/2006/01 Drainage Improvement Works in Sai Kung has commenced constructional activity. It was of main concern to ascertain if there was any undesirable effect of the construction activities on the air quality, noise level and water quality over the construction site and on nearby designated sensitive receivers. Impact environmental monitoring on noise level and water quality was undertaken throughout this review period to acquire data for accessing any potential impact associated with the construction activities on the environment.

<u>Air Quality</u>

Ad hoc air quality monitoring at the project site will only be conducted by ET when instructed by the ER/IC(E) or on receipt of complaint. Nonetheless, the Contractor was advised to be vigilant of any dusty activities and implement prompt dust suppression measures as necessary at potential dust generation areas as to alleviate the contribution of on-going construction activities to a minimum.

Noise Level

Noise level monitoring at the project site was conducted on 3^{rd} to 26^{th} November 2009 on eight occasions during this reporting period. Monitoring comprising of one set of L₁₀, L₉₀ and Leq(30min) measurements was undertaken on each weekday monitoring date.

The monitoring results indicated that the measured noise levels were well below the Limit Level of 75dB(A) during daytime on normal weekdays. Construction sourced activity was not considered influencing any nuisance impact to the sensitive receivers. Noise emanating from vehicular road traffic was found to be the major influential factor dominating the environment.

Water Quality

The water quality monitoring comprising monitoring of dissolved oxygen level, dissolved oxygen saturation, water temperature, turbidity, suspended solids and pH were conducted on two days per week at four downstream monitoring stations (W2, W3, W5 and W7). Impact water quality monitoring in this reporting month was carried out on 3rd to 26th November 2009. Non-compliance events of suspended solids were recorded on 10, 17 and 24 November 2009. The cause of exceedance was attributable to (1) Disturbance of water quality by earth works (2) Surface run off along the river channels after raining and (3) Prevailing water quality in which soil deposited along the riverbed bought up into the existing water body under the influence of tidal effect and natural seasonal variations. The Contractor was urged to implement necessary mitigation measures so as to minimize the impact on the water body.

<u>Complaints</u>

As far as the complaint on the construction work in respect of environmental protection and pollution control was concerned, there was no complaint received during this reviewed session.

Since the commencement of the captioned project. There were two verbal and seven documented complaints received by the Contractor and the Engineer.

Waste Management

For dealing with wastes generated at the site, the contractor has been advised to follow the guideline in Appendix 2.

Impact Prediction Review

Construction activities of grasscrete and retaining wall will proceed in December 2009. It is forecasted that these works may impose slight degree of air, noise and water impact on the sensitive receivers. The Contractor was hence advised to implement necessary mitigation measures and effective surveillance program so as to prevent deterioration of the existing environment.

2. Introduction

This monthly report reviews the progress of the environmental monitoring and audit work associated with the construction works for contract number DC/2006/01 Drainage Improvement Works in Sai Kung for November 2009 and forecasts the activities for December 2009. The monitoring results for noise and water parameter along with their graphical plots are shown in Appendix 4 and Appendix 5 respectively.

3. General Review

3.1 Background

The Drainage Services Department (DSD) of the Hong Kong Special Administrative Region Government has commissioned the drainage improvement works in Sai Kung under Contract No. DC/2006/01.

The location of the project site is shown in Figure 1.1of Appendix 8.

The project commence in July 2007 with the duration of the contract for the civil works approximately 24 months and scheduled for completion in July 2009.

The Contract for the construction works under Contract No. DC/2006/01 was awarded to Sum Kee Construction Limited.

MateriaLab Division of Fugro Technical Services Limited, was requested by Sum Kee Construction Limited to carry out the environmental monitoring and audit (EM&A) in connection with the project works.

The major works items under this contract comprise the following:

- (A) Sai Kung River and Sha Ha Culvert :
- (i) Construction of approximately 150m long of trapezoidal using gabion lining with planting pits and natural substrates and rip-rap bedding; and
- (ii) Construction of approximately 280m long three cells 3m x 3m culvert to connect sai Kung River to the downstream box culvert.
- (B) Ho Chung Channel :
- (i) Construction of approximately 300m long of trapezoidal using gabion lining with planting pits and natural substrates and rip-rap bedding; and
- (ii) Construction of approximately 350m long of rectangular channel by bored pile with natural substrates and rip-rap bedding; and
- (iii) Reprovision of three pedestrian crossing;
- (iv) Reconstruction of existing vehicular crossing and weir arrangement adjacent to WSD to Ho Chung Lowland Pumping Station.
- (C) Pak Kong River :
- (i) Reprovision of one pedestrian and one vehicular crossing to 3-cell box culvert.
- (ii) Construction of approximately 100m long retaining walls to stabilize an existing river slope adjacent to the Hiram's Highway.

The project organization with respect to environmental protection works is shown in Figure 3.2, which indicates responsibilities and lines of communication of the various parties concerned. The organization chart of the Environmental Team is shown in Figure 3.3.




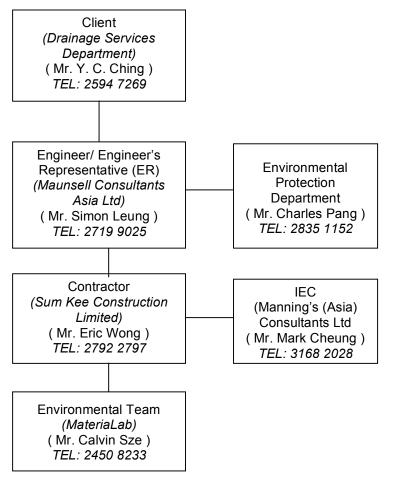


Figure 3.3 Organization Chart of Site Environmental Team

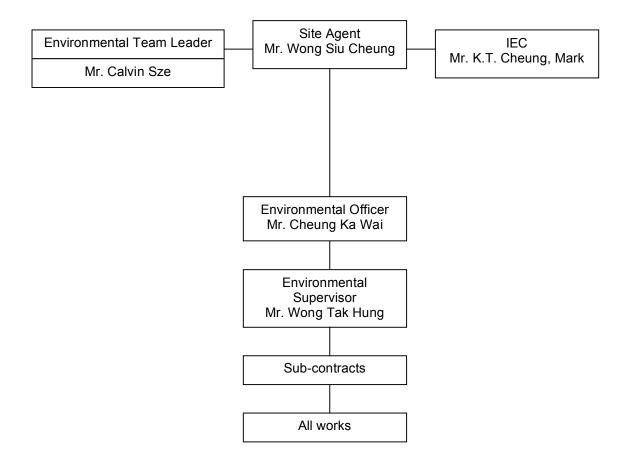

3.2 Summary of Environmental Monitoring and Audit (EM&A) Requirements

The EM&A programme requires the monitoring of air quality, noise level and water quality at the pre-agreed monitoring stations prior to the commencement of construction activities at the project site. During the course of construction, impact monitoring of air quality, noise levels and water quality will be undertaken at the designated monitoring stations in accordance to the active site works area(s) in operation. The requisite monitored parameters are summarised in Table 3.1.

Environmental auditing on the monitoring data is to be undertaken via the establishment of a set of quality performance limits known as Action/Limit (AL) levels for the environmental parameters in concern to check against any exceedances.

The AL levels are summarised in Table 3.2, Table 3.3 and Table 3.4 and their derivations are detailed in the Baseline Environmental Monitoring Report.

Should the monitoring results indicate any non-compliance of the concerned Action/Limit (AL) levels, actions according to the event action plans for air, noise and water in Appendix 6 should be followed and appropriate environmental mitigation measures as shown in Appendix 1 are to be implemented to rectify the situation.

Advice in regard to the implementation status of the environmental protection and pollution control mitigation measures are shown in Appendix 3.

Parameter	Monitoring Items	Number of Stations	Frequency	Requirements
Ad hoc Impact Monitoring for Air	Total suspended particulates (TSP)	3	When required by the ER or IC(E) during the course of the works	1 x 24-hour sampling and 3 x 1-hour sampling
Noise	Daytime noise level of L _{Aeq} (30min)	6	Once per week	1 x Leq (30 min.) between 0700 and 1900 on normal weekdays.
Water	DO, DOS, PH, Turbidity Temp, SS	4	Twice per week in the first three months, then once per week if no exceedances occur	A set of measurements on normal weekdays.

Table 3.1Summary of Monitored Parameters

3.3 Action and Limit Levels

<u>Air Quality</u>

The Action and Limit levels for 1-hour and 24-hour total suspended particulate (TSP) are formulated from the baseline monitoring data. The quality performance levels are shown in Table 3.2.

Location	1-hour TS	6P (μg/m³)	24-hour TSP (μg/m³)				
Location	Action Level	Limit Level	Action Level	Limit Level			
HCAM	346	500	195	260			
PKAM	293	500	160	260			
SKAM	291	500	149	260			

Table 3.2 Action and Limit Level for Air Quality

Noise Level

The 'Action' and 'Limit' levels for noise is based on the number of complaints received during construction and the specified noise limits. The 'Action' and 'Limit' levels are shown in Table 3.3

Table 3.3Action and Limit Level for Construction Noise

Time Period	Action Level	Limit Level, dB (A)	
0700-1900 hrs on normal weekdays	When one documented complaint is received	75*	

* - reduce to 70dB(A) for schools and 65dB(A) during school examination periods.

Water Quality

The Action and Limit levels for the respective water quality parameters are formulated as follows:

Parameter	Station	Action	Limit
	W2	5	
DO in mg/L	W3	5	4
(mid-depth)	W5	6	4
	W7	5	
	W2	27	39
SS in mg/l	W3	27	39
(mid-depth)	W5	12	21
	W7	7	9
Turbidity in	W2	50	63
Turbidity in NTU (mid-depth)	W3	50	63
	W5	9	14
	W7	11	18

Table 3.4 Calculated Action and Limit Levels

Remark:

1. For DO, Non-compliance occurs when monitoring result is lower than the limits.

2. For SS and turbidity, non-compliance occurs when monitoring result is higher than the limits.

4. Construction Phase Environmental Monitoring

4.1. Review of the Construction Phase Monitoring Programme

The schedule for the monitoring programme in this review month, November 2009 is shown in Table 4.1.

SUN	MON	TI	UE	WED	Т	ΉU	FRI	SAT
1	2	3	N,W	4	5	N,W	6	7
8	9	10	N,W	11	12	N,W	13	14
15	16	17	N,W	18	19	N,W	20	21
22	23	24	N,W	25	26	N,W	27	28
29	30							

 Table 4.1
 Environmental Monitoring Schedule For This Review Month

Legend: The sampling date is shaded

- N Noise Monitoring (1 x Leq 30 minute) at 6 locations in two days.
- W Monitoring of DO, DOS, turbidity, pH, temperature and SS at mid-water depth of W2, W3, W5 and W7
- 4.2 Monitoring Locations

Air Quality

Impact air quality monitoring is performed at three locations. The locations of the monitoring station selected as the nearest nearby air sensitive receiver is listed in Table 4.2 and shown in Figures 2.2, 4.1 and 4.2 of Appendix 8.

Designation	Air Quality Monitoring Station
HCAM	At the side of Ho Chung Store on Ho Chung Road roadside
PKAM	At the side of door No. 14 at Fung On Village, Tai Chung Hau
SKAM	At the side of door No. 17 at Wang Kong Village

 Table 4.2 Air Quality Monitoring Stations

<u>Noise Level</u>

Impact noise level monitoring is performed at six locations. The locations of the monitoring stations selected as the nearest nearby noise sensitive receiver is listed in Table 4.3 and shown in Figures 3.2 and 4.2 of Appendix 8.

Table 4.3 Noise Level Monitoring Stations

Designation	Noise Level Monitoring Station
HCM1	In front of door No. 5B, 1 st Lane at Ho Chung Village
HCM2	In front of door No. 107 at Ho Chung New Village
PKM1	At the side of door No. 14 at Fung On Village, Tai Chung Hau
PKM2	In front of Green House Nursery at Pak Kong Riverside
SKM1	In front of door No. 13 at Muk Min Shan
SKM2	In front of Waste Recycling Site at Muk Min Shan

Water Quality

The monitoring work was carried out at the mid-water depth of the four impact monitoring stations downstream of the construction work, W2, W3, W5 and W7, at the Ho Chung River, Pak Kong River and Sai Kung River. The exact locations of the water quality monitoring stations are shown in Figures 4.1, 4.2 and 4.3.

4.3 Monitoring Methodology

Air Quality

The 1-hour and 24-hour TSP levels are measured with a high volume sampler following the standard method as set out in the Title 40 of the Code of Federal Regulations (U.S.), Chapter 1 (Part 50), Appendix B.

The total suspended particulate is sampled by drawing air through a piece of conditioned and pre-weighed filter paper inside the high volume sampler at controlled flowrate of about 40-60 c.f.m. After sampling, the filter paper with the retained particulate is then kept in a plastic bag and transported back to the laboratory for further conditioning and weighing. The TSP level is calculated from the ratio of the mass of particulate retained on the filter to the total volume of air sampled.

Noise level

The impact noise monitoring is carried out at the six monitoring stations selected as the nearest nearby noise sensitive receiver (NSR). Measurement of one L_{Aeq} 30min. should be conducted at each of the monitoring stations on one occasion every week during normal construction working daytime hours (0700 to 1900 hours) (Monday to Saturday).

Noise measurement should be made in terms of the A-weighted equivalent continuous sound pressure level (Leq) measured with an integrating sound level meter complying with International Electrotechnical Commission Publications 651:1979 (Type 1) and 804:1985 (Type 1).

Where a measurement is to be carried out at a building, the assessment point shall normally be at a position 1 metre from the exterior of the building façade. The assessment point shall be at a position 1.2 metre above the ground at a place other than a building.

Immediately prior to and following each noise measurement, the accuracy of the sound level meter is checked using an acoustic calibrator generating a known sound pressure level at a known frequency. Measurements may be accepted as valid only if the calibration levels from before and after the noise measurements agree to within 1.0 dB.

Noise measurement should not be made in the presence of fog, rain, wind with a steady speed exceeding 5 m/s, or wind with gusts exceeding 10m/s.

Water Quality

Water quality monitoring is carried out two times a week at the first three months at four downstream monitoring stations (W2, W3, W5 and W7). Dissolved oxygen level, dissolved oxygen saturation, water temperature, pH value and turbidity (NTU) are measured in-situ at the monitoring stations, while the suspended solids level is ascertained by laboratory analysis.

The parameters of in-situ measurements include water depth, dissolved oxygen (DO), dissolved oxygen saturation (DOS), turbidity level, pH value and water temperature. Water samples is collected by the water sampler and filled into HDPE bottles for laboratory determination of suspended solids. Bottles are filled up to the rim, capped tightly and labeled immediately. The samples are delivered to the laboratory as soon as possible for subsequent analysis.

4.4 Monitoring Equipment

The equipment employed for the requisite monitoring and their respective updated calibration details are summarised in Appendix 7.

4.5 Summary of non-compliance of the environmental quality performance limit for November 2009.

<u>Noise Level</u>

No non-compliance was record for the noise monitoring between 0700 and 1900 hours on normal weekdays. The range and variation of the daytime noise level were compliant to the limit level, which indicating that the construction noise did not engender significant nuisance to the sensitive receivers. Noise emanating from vehicular road traffic was found to be the major influential factor dominating the environment.

Water Quality

Non-compliance regarding suspended solids was recorded when compared with the established baseline criteria were reported in this review period. The summary of non-compliance is listed in Table 4.4.

Date	Location	Parameter	Level of Exceedance	Causes
10/11/2009	W3	Suspended Solids	Limit Level	Disturbance of water quality by earth works
17/11/2009	W3	Suspended Solids	Action Level	Surface runoff along the river channels after raining
17/11/2009	W7	Suspended Solids	Action Level	Surface runoff along the river channels after raining
24/11/2009	W3	Suspended Solids	Action Level	Prevailing water quality in which soil deposited along the riverbed bought up into the existing water body under the influence of tidal effect and natural seasonal variations

Table 4.4 Summary of Non-compliance for Water Quality

4.6 Review of the events of non-compliance

Full compliance of noise level monitoring was recorded in this reporting period.

Regarding the non-compliance of water quality monitoring, the scenario was subject to (1) Disturbance of water quality by earth works (2) Surface run off along the river channels after raining and (3) Prevailing water quality in which soil deposited along the riverbed bought up into the existing water body under the influence of tidal effect and natural seasonal variations.

5. Construction Site Environmental Audit

Site Audit

Site audit is necessary as to ensure:

- No unacceptable practice on site
- · Identification of potential impacts associated with construction activities
- Mitigation measures being properly implemented.
- Implementation of additional mitigation measures of necessary.

Environmental site inspection undertaken weekly by the Contractor's ET Team during this review month with the observations/ deficiencies summarised below:

Summary of recommendations:

- 1. Maintain site housekeeping. Regularly clear and dispose of construction and general waste in timely manner.
- Provide covering and bunding for temporarily stored stockpiles or exposed areas to prevent surface runoff (especially in rainy days) and minimise dust impact when necessary.
- 3. Keep regular water spraying on dry and exposed areas (e.g. haul road and access road) to prevent fugitive dust emission.
- 4. Provide sandbag barrier at site boundary areas to prevent possible runoff in rainy days.
- 5. Treat the discharged water properly before entering the river channels.
- 6. Stagnant water on site areas should be cleared regularly.
- 7. Provide water spraying when concrete breaking is conducting.
- 8. Enclose the active working areas near band with silt curtains / geotextile as necessary.
- 9. Clear the muddy water on haul road to prevent surface run-off discharging to watercourse.
- 10. Leaked lubrication oil should be collected and disposed as chemical waste by licensed collector.
- 11. Deploy hardcore on haul road to suppress fugitive dust emission.
- 12. Clear the deposited soil in drainage channel.

6. Summary of Complaints, Summons and Successful Prosecutions

No complaints and summons in association of environmental performance and pollution control were registered in this reporting month.

Since the commencement of the captioned project. There were two verbal and seven documented complaints but no successful prosecutions received by the Contractor and the Engineer.

7. Works Programme for December 2009

Substantial completion for Pak Kong River, Sai Kung River and Sha Ha Culvent was issued by the Engineer. The principal activities on site for December 2009 are updated and listed as follows:

- Construction of grasscrete at Sha Ha
- Construction of retaining wall at Ho Chung

8. Monitoring Schedule for December 2009

For the forthcoming period, water quality and noise level impact monitoring are to be conducted, with the monitoring schedule shown in Table 8.1.

	Environmen								
SUN	MON	TUE	WED	THU	FRI	SAT			
		1 N,W	2	3 N,W	4	5			
6	7	8 N,W	9	10 N,W	11	12			
13	14	15 N,W	16	17 N,W	18	19			
20	21	22 N,W	23	24 N,W	25	26			
27	28 N,W	29	30 N,W	31					

 Table 8.1
 Environmental Monitoring Schedule for the Forthcoming Month

Legend: The sampling date is shaded

N - Noise Monitoring (1 x Leq 30 minute) at 6 locations in two days

W- Water Monitoring of DO, DOS, turbidity, pH, temperature and SS at mid-water depth of W2, W3, W5 and W7

9. Comments and Conclusions for November 2009

<u>Air Quality</u>

Ad hoc air quality monitoring at the project site will only be conducted by ET when instructed by the ER/ IC(E) or on receipt of complaint. Nevertheless, the Contractor should deploy necessary dust mitigation measures to reduce potential impacts from constructional works to a minimum, which include frequent water spraying at dust generation areas.

Noise Level

During this review month, noise levels around the project were compliant to the limit level with insignificant nuisance on the local environment. Construction sourced noise was not of prominent contribution whereby the surrounding environment which dominated by the vehicular traffic traversing the public roadways was registered.

Water Quality

During this reviewed month, non-compliances of suspended solids were recorded on 10, 17 and 24 November 2009 according to the established levels. The cause was substantially attributable to (1) Disturbance of water quality by earth works (2) Surface run off along the river channels after raining (3) Prevailing water quality in which soil deposited along the riverbed bought up into the existing water body under the influence of tidal effect and natural seasonal variations. The Contractor was urged to conduct necessary mitigation measures so as to keep the disturbance on water quality to minimal levels.

MateriaLab Ref. No. :075117EN90615

Appendix 1

Environmental Mitigation Measures

Air Quality Mitigation Measures

The Contractor shall be responsible for the design and implementation of these measures.

Below is a list of dust mitigation measures specified in the Contract specifications:

Work Area	Recommended Mitigation Measures
Sai Kung River	Twice daily watering of the work site with active operations (material
	handling and haul roads) when the weather and the work site are dry.
	Twice daily watering of the work site with active operations (material
Pak Kong River	handling and haul roads) when the weather and the work site are dry.
Fak Kung Kiver	Extensive watering of the haul roads (at least every two hours daily) to
	keep the haul roads in wet condition.
	Twice daily watering of the work site with active operations (material
Ho Chung	handling) when the weather and the work site are dry.
Channel	Extensive watering of the haul roads (at least every two hours daily) to
	keep the haul roads in wet condition.

- The dust control measures stipulated in the Air Pollution Control (Construction Dust) Regulation shall be incorporated in the contract specifications. These shall be implemented during construction in order to reduce dust impact to within the acceptable criteria of 500mgm⁻³. Typical control measures are:
- > skip hoist for material transport should be totally enclosed by impervious sheeting;
- every vehicle should be washed to remove any dusty materials from its body and wheels before leaving the construction site;
- the area where vehicle washing takes place and the section of the road between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;
- where a site boundary adjoins a road, streets or other accesses to the public, hoarding of not less than 2.4 m high from ground level should be provided along the entire length except for a site entrance or exit;
- all dusty materials should be sprayed with water prior to any loading, unloading or transfer operation so as to maintain the dusty materials wet;
- > all stockpiles of aggregate or spoil should be covered and water applied;
- the height from which excavated materials are dropped should be controlled to a minimum practical height to limit fugitive dust generation from unloading; and
- the load of dusty materials carried by vehicle leaving a construction site should be covered entirely by clean impervious sheeting to ensure dust materials do not leak from the vehicle.

In addition, the speed of haul road traffic should be limited to 10 km per hour.

The following odour control measures are recommended in the EIA Report:

- > any odorous dredged material should be placed remote from air sensitive receivers;
- any odorous permitted stockpiled material should be removed within two days of work to reduce the amount of time available for decomposition; and
- > any odorous permitted stockpiled material should be covered with plastic tarpaulin sheets.

 If the above measures are not sufficient to restore the air quality to acceptable levels upon the advice of ET Leader, the Contractor shall liaise with the ET Leader on some other mitigation measures, propose to ER for approval, and implement the mitigation measures.

Noise Mitigation Measures

The Contractor shall be responsible for the design and implementation of these measures:

- Use of quiet Powered Mechanical Equipment (PME)
- Use of movable noise barriers
- Use of temporary noise barriers

If the above measures are not sufficient to restore the construction noise quality to acceptable levels upon the advice of ET Leader, the Contractor shall liaise with the ET Leader on some other mitigation measures, propose to ER and IC(E) for approval, and carry out the mitigation measures

Water Quality Mitigation Measures

The Contractor shall be responsible for the design and the implementation of these measures.

Below is a list of water mitigation measures specified in the Contract specifications :

Construction Phase

Channel Excavation Works

- Regarding to the impacts on water quality, it is very important to properly schedule the construction activities. The excavation works for the earth channel construction would be carried out along the three streams. Wet excavation should be reduced as much as possible. Due to the characteristics of narrow width and small water flow of the original channel, the excavation can be carried out in dry condition (even in wet season) by diverting the stream flow from upstream by a temporary drainage channel or narrowing the river/stream with a temporary earth bund or barrier. Containment measures such as bunds and barriers should be used within the river/stream to prevent water from entering the excavation area. The temporary drainage channel would be backfilled when the construction works are completed or the temporary diversion is no longer required. Although flooding of the proposed contaminant section seldom occurs during the dry season, the excavation would consider to temporarily stop when flood water enter the containment causing leakage of runoffs to stream water.
- To further minimise the leakage and loss of sediments during excavation, tightly sealed closed grab excavators should be employed in river sections where material to be handled is wet. Where material is dry and in non-river sections, conventional excavations can be used.

Construction Run-off and Drainage

The site practices outlined in *ProPECC PN 1/94 "Construction Site Drainage*" should be followed as far as practicable in order to minimise surface runoff and the chance of erosion, and also to retain and reduce any suspended solids prior to discharge. These practices include the following items:

- Before commencing any site formation work, all sewer and drainage connections should be sealed to prevent debris, soil, sand etc. from entering public sewers/drains.
- Temporary ditches should be provided to facilitate run-off discharge into appropriate watercourses, via a silt retention pond.
- Boundaries of earthworks should be marked and surrounded by dykes or embankments for flood protection, as necessary.

- Sand/silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove sand/silt particles from runoff to meet the requirements of the Technical Memorandum standard under the Water Pollution Control Ordinance. The design of silt removal facilities should be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures should be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms.
- Water pumped out from foundation excavations should be discharged into silt removal facilities.
- Careful programming of the works to minimise surface excavations for the drainage improvement works during the wet season. If excavation of soil cannot be avoided during the wet season, exposed slope surfaces should be covered by a tarpaulin or other means. Other measures that need to be implemented before, during, and after rainstorms are summarizeised in ProPECC PN 1/94.
- Exposed soil areas should be minimizeised to reduce potential for increased siltation and contamination of runoff.
- Earthwork final surfaces should be well compacted and subsequent permanent work should be immediately performed.
- Open stockpiles of construction materials or construction wastes on-site should be covered with tarpaulin or similar fabric during rainstorms.

General Construction Activities

- Debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering the adjacent watercourses. Stockpiles of cement and other construction materials should be kept covered when not being used.
- Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to the river/streams, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event.

Sewage from Construction Workforce

 Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities.

Operation Phase

 Desilting of the three river channels should be carried out during periods of low flow (i.e. dry season, from November to March).

Accidental Spillage of Chemicals on Site

- In case of the occurrence of accidental spillage of chemicals, it is required to take immediate actions to control the release of chemicals into the nearby water bodies. It is recommended that the contractor of the project should develop an emergency plan to deal with accidental spillage of chemicals in the construction site.
- Good site practices would avoid the accidents to occur. Areas for chemical storage should be securely locked and kept as far from the drainage systems or stream courses as possible. The storage area should have an impermeable floor and bunding of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest, to minimise the impacts from any potential accidents.
- Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste Disposal Ordinance details the requirements to deal with chemical wastes. General requirements are given as follows:
- Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport;
- Chemical waster containers should be suitably labelled to notify and warn the personnel who are handling the wastes to avoid accidents; and
- Storage area should be selected at a safe location on site and adequate space should be allocated to the storage area.

MateriaLab Ref. No. :075117EN90615

Appendix 2

Waste Management Guideline

Waste Management

Below is a list of waste material mitigation measures specified in the Contract specifications:

Good Site Practices and Waste Reduction Measures

- Appropriate waste handling, transportation and disposal methods for all waste arisings generated during the construction works shall be implemented to ensure that construction wastes do not enter the river and stream channels.
- It is expected that adverse impacts from waste management would not arise, provided that good site practices are strictly followed. Recommendations for good site practices during construction to be carried out by the Contractor include:
- nomination of approved personnel, such as a site manager, to be responsible for good site practices, and making arrangements for collection of all wastes generated at the site and effective disposal to an appropriate facility;
- training of site personnel in proper waste management and chemical waste handling procedures;
- > provision of sufficient waste disposal points and regular collection for disposal;
- appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers;
- separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility;
- regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors;
- a recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) should be proposed; and
- a Waste Management Plan shall be prepared by the Contractor and submitted to ER for approval. One may make reference to ETWB TCW No. 15/2003 for details.
- In order to monitor the disposal of C&D material at landfills and public filling areas, as appropriate, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements to be implemented by the Contractor and audited by the ET. One may make reference to ETWB TCW No. 31/2004 for details.
- Good management and control can prevent the generation of significant amounts of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction to be carried out by the Contractor include:
- segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;
- to encourage collection of aluminium cans by individual collectors, separate labelled bins shall be provided to segregate this waste from other general refuse generated by the work force;

- > any unused chemicals or those with remaining functional capacity shall be recycled;
- > maximising the use of reusable steel formwork to reduce the amount of C&D material;
- prior to disposal of C&D waste, it is recommended that wood, steel and other metals shall be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill;
- proper storage and site practices to minimise the potential for damage or contamination of construction materials; and
- plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.
- In addition to the above good site practices and waste reduction measures, specific mitigation measures are recommended below for the identified waste arisings to minimise environmental impacts during handling, transportation and disposal of these wastes.

Construction and Demolition Material

- The C&D material generated from the river improvement works would comprise public fill, being excavated soil and small rocks. To minimise off-site disposal of public fill, the excavated material with suitable characteristics/size should be reused on-site as fill material as far as practicable, such as for backfilling of temporary drainage channels or construction of embankments, and small cobbles and rocks should be used in the construction of the recreated channel bed.
- When disposing C&D material at a public filling area, it shall be noted that the material shall only consist of soil, rock, concrete, brick, cement plaster/mortar, inert building debris, aggregates and asphalt. The material shall be free from marine mud, household refuse, plastic, metals, industrial and chemical waste, animal and vegetable matter, and other material considered to be unsuitable by the Filling Supervisor.
- The C&D material generated from demolition of existing structures should be sorted on-site into inert C&D material (that is, public fill) and C&D waste. The proposed disposal sites for the public fill and C&D waste are the Fill Bank at Tseung Kwan O Area 137 and SENT Landfill, respectively. Suitable areas should be designated within the works site boundaries for temporary stockpiling of C&D material. Within stockpile areas, the following measures should be taken to control potential environmental impacts or nuisance:
- covering material during heavy rainfall;
- > locating stockpiles to minimise potential visual impacts; and
- > minimising land intake of stockpile areas as far as possible.

Excavated Riverbed Material

It is anticipated that the excavated riverbed material may need to be temporarily stockpiled on-site prior to disposal off-site. Details of environmental control measures to be taken at the stockpiling area to prevent water pollution are discussed in *Section 4*. Use of water-tight trucks would be required for the transportation of excavated riverbed material to the designated barging point for disposal at the designated public filling area, or transported directly to the public filling area. The proposed disposal site for the excavated material is the Fill Bank at Tseung Kwan O Area 137.

Chemical Wastes

If chemical wastes are produced at the construction site, the Contractor shall be required to register with the EPD as a Chemical Waste Producer and to follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes should be used, and incompatible chemicals should be stored separately. Appropriate labels should be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosives, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes generated at the Chemical Waste Treatment Centre at Tsing Yi, or other licensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.

General Refuse

 General refuse should be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector shall be employed by the Contractor to remove general refuse from the site, separately from C&D material. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material.

MateriaLab Ref. No. :075117EN90615

Appendix 3

Environmental Mitigation Measures Implementation Schedule

Environmental Mitigation Measures Implementation Schedule

Air Quality

EIA Ref [#]	Environmental Mitigation Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages			Relevant Legislation and Guidelines
				Des	С	0	and Guidennes
\$3.8.4	 <u>Sai Kung River</u> Twice daily watering of the work site with active operations (material handling and haul roads) when the weather and the work site are dry. <u>Ho Chung Channel and Pak Kong River</u> Twice daily watering of the work site with active operations (material handling) when the weather and the work site are dry. Extensive watering of the haul roads (at least every two hours daily) to keep the haul roads in wet condition 	Work site / During construction period	Contractor		~		Air Pollution Control (Construction Dust) Regulation
S3.8.6	Dust mitigation measures stipulated in the Air Pollution Control (Construction Dust) Regulation shall be incorporated to control dust emission. Notice shall be given to the authority prior to commencement of works.	Work site / During construction period	Contractor		~		Air Pollution Control (Construction Dust) Regulation
S3.8.7	The speed of haul road traffic should be limited to 10 kph	Work site / During construction period	Contractor		~		Air Pollution Control (Construction Dust) Regulation
S3.8.8	 To minimise odour nuisance at nearby ASRs, the following odour control measures are recommended: any odorous dredged material should be placed remote from air sensitive receivers; any odorous permitted stockpiled material should be removed within two days of work to reduce the amount of time available for decomposition; and any odorous permitted stockpiled material should be covered with plastic tarpaulin sheets 	Work site / During construction period	Contractor		~		Air Pollution Control (Construction Dust) Regulation

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project. * Des - Design, C - Construction, and O – Operation, and Dec - Decommissioning

Noise Level

EIA Ref [#]	Environmental Mitigation Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages			Relevant Legislation and Guidelines
				Des	с	ο	and Guidennes
S 4.8.1-S4.8.3	Use of quiet PME	Work site / During the construction period	Contractor		~		ProPECC PN2/93 and Noise Control Ordinance
S 4.8.4-S4.8.10	Use of movable noise barriers and temporary noise barrier	Work site / During the construction period	Contractor		~		ProPECC PN2/93 and Noise Control Ordinance
S 4.8.11	 Good Site Practice Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction program; Silencers or mufflers on construction equipment should be utilised and should be properly maintained during the construction program; Mobile plant, if any, should be sited as far from NSRs as possible; Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 	Work site / During the construction period	Contractor		~		ProPECC PN2/93 and Noise Control Ordinance
S4.10.1	Environmental Monitoring and Audit (EM&A) programme is recommended to be implemented during the construction stage.	Work site / During the construction period	Contractor		~		-

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project. * Des - Design, C - Construction, and O – Operation, and Dec - Decommissioning

Water Quality

EIA Ref [#]	Environmental Mitigation Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages		tion	Relevant Legislation
				Des	С	0	and Guidelines
S5.8.2 –S5.8.3	 Channel Excavation Works Excavation to can be carried out in dry condition (even in wet season) by diverting the stream flow from upstream by a temporary drainage channel or narrowing the river/stream with a temporary earth bund or barrier. Containment measures such as bunds and barriers should be used within the river/stream to prevent water from entering the excavation area. Tightly sealed closed grab excavators should be employed in river sections where material to be handled is wet. Where material is dry and in non-river sections, conventional excavations can be used. 	Work site / During the construction period	Contractor		~		-
S5.8.5	 Construction Runoff and Drainage Before commencing any site formation work, all sewer and drainage connections should be sealed to prevent debris, soil, sand etc. from entering public sewers/drains. Temporary ditches should be provided to facilitate run-off discharge into appropriate watercourses, via a silt retention pond. Boundaries of earthworks should be marked and surrounded by dykes or embankments for flood protection, as necessary. Sand/silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove sand/silt particles from runoff to meet the requirements of the Technical Memorandum standard under the WPCO. The design of silt removal facilities should be based on the guidelines provided in ProPECC PN 1/94. All drainage facilities and erosion and sediment control structures should be inspected monthly and maintained to ensure proper and efficient operation at all times and particularly during rainstorms. Water pumped out from foundation excavations should be discharged into silt removal facilities. Careful programming of the works to minimise surface excavations for the drainage improvement works during the wet season. If excavation of soil cannot be avoided during the wet season. If excavation of soil cannot be avoided to ProPECC PN 1/94. Exposed soil areas should be minimised to reduce potential for increased siltation and contamination of runoff. Earthwork final surfaces should be well compacted and subsequent permanent work should be immediately performed. Open stockpiles of construction materials or construction wastes onsite should be covered with tarpaulin or similar fabric during rainstorms. 	Work site / During the construction period	Contractor				ProPECC PN 1/94; WPCO

Water Quality (continued)

EIA Ref [#]	Environmental Mitigation Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages	Relevant Legislation and Guidelines
S5.8.6-S5.8.7	 General Construction Activities Debris and refuse generated on-site should be collected, handled and disposed of properly to avoid entering the adjacent watercourses. Stockpiles of cement and other construction materials should be kept covered when not being used. Oils and fuels should only be used and stored in designated areas which have pollution prevention facilities. To prevent spillage of fuels and solvents to the river/streams, all fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. The bund should be drained of rainwater after a rain event. 	Work site / During the construction period	Contractor		ProPECC PN 1/94; WPCO
S5.8.8	 Sewage from Construction Workforce Temporary sanitary facilities, such as portable chemical toilets, should be employed on-site where necessary to handle sewage from the workforce. A licensed contractor would be responsible for appropriate disposal and maintenance of these facilities. 	Work site / During the construction period	Contractor		WPCO

Water Quality (continued)

EIA Ref [#]	Environmental Mitigation Measures / Mitigation Measures	Location / Timing	Implementation Agent	Implementation Stages	Relevant Legislation and Guidelines
S5.8.10- S5.8.12	 Accidental Spillage of Chemicals on Site In case of the occurrence of accidental spillage of chemicals, it is required to take immediate actions to control the release of chemicals into the nearby water bodies. It is recommended that the contractor of the project should develop an emergency plan to deal with accidental spillage of chemicals in the construction site. Good site practices would avoid the accidents to occur. Areas for chemical storage should be securely locked and kept as far from the drainage systems or stream courses as possible. The storage area should have an impermeable floor and bunding of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest, to minimise the impacts from any potential accidents. Disposal of chemical wastes should be carried out in compliance with the Waste Disposal Ordinance. The Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes published under the Waste. General requirements are given as follows: Suitable containers should be used to hold the chemical wastes to avoid leakage or spillage during storage, handling and transport; Chemical waster containers should be suitably labelled to notify and warn the personnel who are handling the wastes to avoid accidents; Storage area should be allocated to the storage area. 	Work site / During the construction period			WPCO
S5.10.1	Water quality monitoring requirements and regular audit during construction phase should be carried out.	Drainage channel / During the operation period	Contractor	~	-

All recommendations and requirements resulted during the course of EIA/EA Process, including ACE and / or accepted public comment to the proposed project. * Des - Design, C - Construction, and O – Operation, and Dec - Decommissioning

Waste Management

EIA Ref [#]	Environmental Mitigation Measures / Mitigation Measures	Location / Timing	Implementation		lementat Stages	ion	Relevant Legislation and Guidelines
		Location, mining	Agent	Des	С	0	
S6.5.2 – S6.5.3	 Good Site Practices and Waste Reduction Measures Good site practices during the construction activities include: Nomination of approved personnel, such as a site manager, to be responsible for good site practices and making arrangements for collection of all wastes generated at the site and effective disposal to an appropriate facility. Training of site personnel in proper waste management and chemical waste handling procedures. Provision of sufficient waste disposal points and regular collection for disposal. Appropriate measures to minimise windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers. Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility. Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. A recording system for the amount of wastes generated, recycled and disposed (including the disposal sites) shall be proposed. A Waste Management Plan shall be prepared and submitted to the Engineer for approval. One may make reference to ETWB TCW No. 15/2003 for details. In order to monitor the disposal of C&D materials at landfills and public filling areas, and to control fly tipping, a trip-ticket system shall be included as one of the contractual requirements. One may make reference to ETWB TCW No. 321/20042 for details. 	Work site / During the construction period	Contractor				Waste Disposal Ordinance (Cap.54), WBTC No.21/2002, ETWB TCW No. 15/2003, ETWB TCW No. 31/2004
S6.5.9	Excavated Riverbed Material Use of water-tight trucks for the transportation of excavated riverbed material to the designated barging point for disposal at the designated public filling area, or transported directly to the public filling area. General Refuse	Work site / During the construction period	Contractor		~		WDO

Waste N	Management	(continued)
---------	------------	-------------

FIA RET	Environmental Mitigation Measures / Mitigation	Location / Timing	Implementation	n Implementati N Stages		ion	Relevant Legislation
	Measures	Location / Thining	Agent	Des	С	0	and Guidelines
S6.5.11	General Refuse General refuse shall be stored in enclosed bins or compaction units separate from C&D material. A reputable waste collector shall be employed by the contractor to remove general refuse from the site, separately from C&D material. An enclosed and covered area is preferred to reduce the occurrence of 'wind blown' light material.	Work site / During the construction period	Contractor		~		Public Health and Municipal Services Ordinance (Cap. 132)
S6.5.10	Chemical Waste If chemical wastes are produced at the construction site, the Contractor shall register with the EPD as a Chemical Waste Producer and follow the guidelines stated in the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Good quality containers compatible with the chemical wastes shall be used, and incompatible chemicals shall be stored separately. Appropriate labels shall be securely attached on each chemical waste container indicating the corresponding chemical characteristics of the chemical waste, such as explosives, flammable, oxidizing, irritant, toxic, harmful, corrosive, etc. The Contractor shall use a licensed collector to transport and dispose of the chemical wastes generated at the Chemical Waste Treatment Centre at Tsing Yi, or other licencedlicensed facility, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation.	Work site / During the construction period	Contractor		~		Waste Disposal (Chemical Waste) (General) Regulation

Land Contamination

EIA Ref [#]	Environmental Mitigation Measures / Mitigation	Location / Timing	Implementation Stages			 Relevant Legislation 	
	Measures	g	Agent	Des	С	0	and Guidelines
S.7.7.2 – S.7.7.3	 Land Contamination Assessment A full site inspection is required by the future Environmental Team immediately after the site was resumed should be undertaken to review the validity of the preliminary CAP and define the exact sampling locations and sampling parameters for further site investigation. An updated CAP shall then be prepared after the site inspection in accordance with EPD's "<i>Guidance Notes for Investigation and Remediation of Contaminated Sites of Petrol Filling Stations, Boatyards, and Car Repair/Dismantling Workshops</i>" and submitted to EPD for approval endorsed by EPD prior to commencement of the site investigation. Upon receipt of EPD's approval on the updated CAP, the actual site investigation for land contamination impact assessment shall be conducted according to the approved CAPly before any construction work started at the identified contaminated sites. A Contamination Assessment Report (CAR) shall be compiled to document the findings and shall include interpretation of laboratory testing results in accordance with the <i>ProPECC Note No. 3/94</i> and comparison of the findings with relevant standards, such as the Dutch guidelines or other international practices as appropriate. If land contamination is confirmed, a Remediation Action Plan (RAP) shall be drawn up to formulate necessary remedial measures and potential water quality impact to the river shall be also addressed if necessary in the remediation measures. The subsequent CAR and RAP shall be endorsed 	Identified areas which require specific contamination investigation /After land resumption and during construction period	Agent Contractor			0	-
	by EPD before implementation of any remedial technology. The contaminated sites should be remediated before commencement of any construction work at the concerned sites which may disturb the ground. The duration of remediation should be taken into account by the Project Proponent or the Contractor as part of the construction programme.						

Land Contamination (c	continued)
-----------------------	------------

EIA Ref [#]	Environmental Mitigation Measures / Mitigation Measures	Location / Timing	Implementation	on Implementation Stages			Relevant Legislation
		J	Agent	Des	С	0	and Guidelines
S.7.9.1	 Mitigation Measures Mitigation measures for handling of the the identified areas contaminated materials are recommended to minimise the potentially adverse effects on the health and safety of construction workers and the impacts arising from the disposal of potentially contaminated materials. These measures include: Construction workers' potential contact with contaminated materials should be minimised by using bulk earth-moving excavator equipment; Exposure to any contaminated materials should be minimised by wearing appropriate clothing and personal protective equipment such as gloves and masks (when interacting directly with suspected contaminated material), providing adequate hygiene and washing facilities and preventing smoking and eating during such activities; Stockpiling of contaminated excavated materials on site should be avoided as far as possible; The use of contaminated soil for landscaping should be prohibited unless there is proper treatment of soil; Vehicles containing any excavated materials should be suitably covered to limit potential dust emissions or contaminated wastewater run-off, and truck bodies and tailgates should be sealed to prevent any discharge during transport or during wet conditions; Only licensed waste haulers should be used to collect and transport any contaminated material to an appropriate disposal site and procedures should be developed to ensure that illegal disposal of waste does not occur; The necessary waste disposal permits should be obtained, as required, from the appropriate authorities, in accordance with the Waste Disposal (Chemical Waste) (General) Regulation (Cap 35), as required; Records of the quantities of wastes generated and disposed of should be maintained; and In accordance with good construction practice, silt traps should be used to reduce the impact of ariange caused by suspended solids arising from disturbed ground, or any construction materials such as	Contaminated sites identified in the CAR / During construction period	Contractor				Waste Disposal Ordinance Waste Disposal (Chemical Waste) (General) Regulation

Ecological Requirements

EIA Ref [#]	Environmental Mitigation Measures / Mitigation Measures	Location / Timing	Implementation	n Implementation Stages			Relevant Legislation
			Agent	Des	С	ο	and Guidelines
S8.7.2 & S8.7.5	 For the Sai Kung River, the base of the improved channel should be lined with natural substrates (e.g., gravel, cobbles and boulders). Substrates found in the existing river section should be used to line the new channel. Substrates lining the improved channel should be arranged to re-create the existing riffle-pool sequence found in the river. Pits would be provided in the gabion to allow planting of herbaceous riparian vegetation. For the Ho Chung River, newly widened sections of riverbed should be lined with natural substrates (e.g., cobbles and boulders), with the size and arrangement of these substrates selected to complement adjacent areas of the existing riverbed. The substrates should be sourced as far as practicable from materials excavated during the river widening. Pits should be provided in the gabion to allow planting of herbaceous riparian vegetation. 	Work site / During planning & design stage, construction stage	Contractor	~	~		-
S8.7.10 & S8.8.5	 At the Sai Kung and Ho Chung Rivers the following measures would be implemented: Drainage improvement works would be limited to downstream sections of the existing rivers. Within the proposed works areas, drainage improvement works would be conducted in sections (approximately 250m in length) along only one bank of the river at a time. Excavation works would be restricted to an enclosed dry section of the river, with containment measures such as bunds and barriers used within the river to minimise the impacts upon the downstream water body. Using this approach to construction works, only localised areas of the river would be subject to disturbance at any one time, and flow would be maintained within the rivers. The excavation works for channels should be carried out in the dry condition, with construction carried out by land-based plant. Excavation works should be restricted to an enclosed dry section of the river, with containment measures such as bunds and barriers used within the rivers. The excavation works for channels should be carried out in the dry condition, with construction carried out by land-based plant. Excavation works should be restricted to an enclosed dry section of the river, with containment measures such as bunds and barriers used within the river to minimise the impacts upon the downstream water body. Site runoff should be directed towards regularly cleaned and maintained silt traps and oil/grease separators to minimise the risk of sedimentation and pollution of river water. The silt and oil/grease separators should be appropriately designed for the local drainage and ground conditions. To minimise leakage and loss of sediments during excavation in narrow channels, tightly sealed closed grab excavators should be deployed where material to be handled is wet 	Work site/during construction phase	Contractor		~		-

EIA Ref [#]	Environmental Mitigation Measures / Mitigation	Mitigation Location / Timing	Implementation		lementat Stages	tion	— Relevant Legislation and	
	Measures		Agent	Des	С	0	Guidelines	
S8.8.6	Noise mitigation measures including the use of quiet construction plant and temporary noise barriers (Section 4 of the EIA report refers) should be implemented to minimise disturbance to habitats adjacent to the works areas. In particular, measures such as noise barriers should be used to minimise disturbance to the bat roost identified close to the Pak Kong works area.	Pak Kong/during construction phase	Contractor		~		-	
S8.8.7	Two small trees and six seedlings of the rare tree species Ehretia acuminata recorded on the southern bank of the existing Ho Chung River to be transplanted to another area within the Ho Chung site boundary before the commencement of construction phase activities. The exact location for transplantation would be confirmed during the design stage. Fencing would be erected around the transplanted trees/seedlings to minimise potential construction phase disturbance.	Ho Chung works site/before construction phase	Contractor		~		-	
S8.8.9	Seeds from the existing Ehritia acuminata trees should be collected and propagated. The seeds should be collected from mature fruits (the fruiting period of E. acuminata is from May to September) prior to transplantation, and germinated in containers under suitable conditions. Following germination and growth, the seedlings should be planted at suitable locations within the Ho Chung Works Area (to be determined during the detailed design stage). The survival of newly planted seedlings should be monitored. Seed collection, propagation, planting and monitoring of E. acuminata should be undertaken by a suitably qualified botanist/horticulturalist appointed by the Project Proponent. A detailed methodology for these works should be formulated during the detailed design stage of the Project, in consultation with AFCD.	Ho Chung works site/before construction phase	Contractor		~		-	
S8.8.14	The improved Ho Chung River is expected to provide a suitable habitat for fish communities previously recorded from the river. To further increase the value of the River for fish communities, it is recommended thatS small fish ladders are to be constructed over the weirs along the river channel. Existing weirs within the river currently impede the movement of fish between upstream and downstream sections of the river. The fish ladders would facilitate movement past these obstacles, extending the range of fish communities in both upstream and downstream areas. The detailed design of the ladders would be submitted to AFCD for comment and approval before finalisation.	Work site / During planning & design stage, and construction stage	Contractor	~	~		-	

Ecological	Requirements	(continued))

EIA Ref [#]	ef [#] Environmental Mitigation Measures / Mitigation Location / Timing Implementation Agent	Location / Timing	Implementation	Implementation Stages			Relevant Legislation and
		Agent	Des	C	0	Guidelines	
S8.8.15- S8.8.16	 Extensive planting of trees and other vegetation along the banks of the newly created channels would be implemented Compensatory planting should make use of native plant species with flowers/fruits attractive to wildlife. 	Works site/during construction phase	Contractor		~		-
S8.10.1	The proper implementation of ecological mitigation measures should be audited. Details are provided in the EM&A Manual.	Works site/during construction phase	Contractor/ET	~	~		-
\$8.10.2- \$8.10.3	 A specific monitoring programme of channels constructed to replace Sai Kung and Ho Chung Rivers is recommended. Details are provided in the EM&A Manual. Contingency plan should be implemented if the post-construction phase monitoring demonstrates that re-colonisation is unsuccessful. Details are provided in the EM&A Manual. 	Works site/before and during construction phase, operation phase	Contractor /Ecologist appointed by Project Proponent (DSD)	~	~	~	-
S8.10.4	Rregular monitoring of the trees and seedlings covering the 12-month period following transplantation and planting should be conducted by a suitably qualified botanist/horticulturalist appointed by the Project Proponent. Details are provided in the EM&A Manual.	Ho Chung works site/before and during construction phase	botanist/ horticulturalist appointed by the Project Proponent (DSD)	~	~		-

Landscape and Visual

EIA Ref [#]	Environmental Mitigation Measures / Mitigation	Location / Timing	Location / Timing Implementation Agent	Implementation Stages			Relevant Legislation and	
	Measures	g		Des	С	0	Guidelines	
Fig A9.12A	 LMM 1 - Gabions with Pits to Plant Riparian Vegetation During detailed design, there should be co-ordination between the designers to ensure that pits are allowed in gabions with sufficient soil for the planting of riparian vegetation. 	Works site/during construction phase	12 months establishment period: Contractor Operation: DSD		~	~	DSD Particular Specification WBTC 2/2004	
Fig A9.12A	 LMM 2 - Rip Rap and Riffles Treatment to Channel Base The channel base should be covered in rip-rap which is considered to be more aesthetically appropriate than fair-faced concrete. Riffles with different water depths should be created incorporating aquatic plants. 	Works site/during construction phase	12 months establishment period: Contractor Operation: DSD		~	~	DSD Particular Specification	
Fig A9.12A	 LMM 3 – Surface Treatment of Flood Walls and Retaining Walls At the design stage, there should be comprehensive planning by the designers to ensure that the appearance of flood walls incorporate aesthetic treatments which is considered to be aesthetically appropriate than fair-faced concrete. 	Works site/before and during construction phase	12 months establishment period: Contractor Operation: DSD		~	~	DSD Particular Specification	
Fig A9.12B	 LMM 4 – Compensatory Planting along Drainage Channel At the detailed design stage, tree and shrub planting should be included by the designer using amenity species along footpath areas or woodland seedling tree and shrub on slopes. 	Works site/during construction phase	12 months establishment period: Contractor Operation: DSD		~	~	WBTC 14/2002 WBTC 2/2004	
Fig A9.12B	 LMM 5 – New Roadside Tree Planting along Access Roads Allowance should be made for planting of heavy standard size trees in the ratio of one tree planted every tree felled 	Works site/during construction phase	12 months establishment period: Contractor Operation: DSD		~	~	WBTC 14/2002 WBTC 2/2004	
Fig A9.12B	 LMM 6 - Grass Concrete Slabs Grass concrete slabs should be used in maintenance access over covered culverts and access ramps to produce a more pronounced greening effect. 	Works site/during construction phase	12 months establishment period: Contractor Operation: DSD		~	~	DSD Particular Specification	

Cultural Heritage

EIA Ref [#]	Environmental Mitigation Measures / Mitigation	Location / Timing	Implementation		lementat Stages	tion	– Relevant Legislation and
	Measures	Looution, mining	Agent	Des	С	0	Guidelines
S10.10.1	The Contractor should report to the Engineer, DSD and the AMO immediately for any discovery of the Antiquities or supposed antiquities during the course of the construction works.	Work site /during construction phase	Contractor		~		Antiquities and Monuments Ordinance
S10.10.2	 Mitigation Measures during Construction Stage <i>Higher earth god shrine:</i> Protective measures should be provided for the shrine if works are taken place in close proximity. The protective measures should consist of the following: High visibility fencing at a distance of one meter around the shrine; and Heavy duty plastic sheeting to be placed over the exterior surfaces of the shrine for duration of ongoing works. A pedestrian access path to the shrine is located within the works area, for purposes of public safety, the path should be marked with a temporary fence and the access route clearly marked by signage. <i>The Che Kung Temple, Ho Chung:</i> Vehicle parking is currently available in an open lot directly to the northwest of the temple. If the works area infringes on the parking area, alternative parking facilities should be more available. Clear signage for directions to the temple should be avoided. If it is unavoidable, any trees that are removed from the area should be replaced by trees of the same species. 	Specified Resources / during construction phase	Contractor		~		

Other EIA Requirements

EIA Ref [#]	Environmental Mitigation Measures / Mitigation	Location / Timing	Implementation		ementat Stages	ion	Relevant Legislation and	
	Measures	Looution, ming	Agent	Des	С	0	Guidelines	
-	 Environmental Monitoring and Audit (EM&A) Site inspection shall be carried out regularly by the Environmental Team (ET) to inspect construction activities to ensure that the recommended environmental protection and pollution control mitigation measures are properly implemented. Details of the requirements and procedures in conducting site inspections are given in the EM&A Manual. On the receipt of any complaints, the Environmental Team Leader (including co-operation s required from other parties) shall promptly undertake investigation work and the necessary actions carried out as based on the results of the investigation. Details of the recommended complaints handling procedures and actions are given in the EM&A Manual. 	Work site /during construction phase	Contractor and ET		~		-	

Appendix 4

Data for Water and Noise Monitoring

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

Our Ref. No.: 075117WA91895

: Sum Kee Construction Limited Client Project

: DC/2006/01 Drainage Improvement Works in Sai Kung

Impact Water Quality Monitoring Field Data Record

Equipment : YSI model DO 200 dissolved oxygen meter (E-004-28) YSI pH meter (E-023-20) HACH 2100P Turbidimeter (E-047-4)

Date (Weather)	Location	Time	Water Depth (m)	Water Temp. (°C)	DO level (mg/L)	DOS (%)	Turbidity (NTU)	pH (unit)	SS (mg/L)	Remarks and Observation
03/11/2009 (Fine)	W2	11:14	0.85	20.8	10.82	120.8	4.46	9.54	2	-
	W3	10:53	0.97	21.7	8.30	94.2	11.2	7.98	11	-
	W5	10;32	1.06	24.4	6.73	80.3	4.03	7.74	7	-
	W7	10:17	2.05	20.6	9.17	101.5	3.44	7.57	5	-

Prepared by : _____S.N. Kong_____

Certified by : Approved Signatory: K.F. Wong

MateriaLab

Date

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

MateriaLab

Our Ref. No.: 075117WA91895

 Client
 : Sum Kee Construction Limited

 Project
 : DC/2006/01 Drainage Improvement Works in Sai Kung

Impact Water Quality Monitoring Field Data Record

Equipment : YSI model DO 200 dissolved oxygen meter (E-004-28) YSI pH meter (E-023-20) HACH 2100P Turbidimeter (E-047-4)

Date (Weather)	Location	Time	Water Depth (m)	Water Temp. (°C)	DO level (mg/L)	DOS (%)	Turbidity (NTU)	pH (unit)	SS (mg/L)	Remarks and Observation
05/11/2009 (Cloudy)	W2	11:18	0.80	24.2	9.58	114.0	3.73	9.13	2	- -
	W3	10:57	0.53	25.0	8.72	105.3	11.2	7.78	14	-
	W5	10:38	0.52	25.4	6.66	81.2	8.10	7.63	9	-
	W7	10:21	1.35	25.3	7.43	90.2	5.74	7.54	7	-

Prepared by : S.N. Kong

Certified by : Approved Signatory: K.F. Wong

Date

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233 Fax : +852-2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk

MateriaLab

Our Ref. No.: 075117WA91895

Client : Sum Kee Construction Limited Project : DC/2006/01 Drainage Improvement Works in Sai Kung

Impact Water Quality Monitoring Field Data Record

Equipment : YSI model DO 200 dissolved oxygen meter (E-004-28) YSI pH meter (E-023-20) HACH 2100P Turbidimeter (E-047-1)

Date (Weather)	Location	Time	Water Depth (m)	Water Temp. (°C)	DO level (mg/L)	DOS (%)	Turbidity (NTU)	pH (unit)	SS (mg/L)	Remarks and Observation
	W2	11:14	0.85	25.5	9.62	122.7	1.80	8.23	<1	-
10/11/2009	W3	10:56	0.10	27.1	7.29	94.6	43.3	7.89	45	Excavation
(Fine)	W5	10:34	0.10	26.7	7.44	95.9	5.41	7.81	3	
	W7	10:10	0.80	27.0	6.91	89.7	5.53	7.46	3	-

Prepared by : _____S.N. Kong_____

Certified by : Approved Signatory: K.F. Wong

GEN01/1208

Date

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

MateriaLab

Our Ref. No.: 075117WA91895

Client : Sum Kee Construction Limited

Project : DC/2006/01 Drainage Improvement Works in Sai Kung

Impact Water Quality Monitoring Field Data Record

Equipment : YSI model DO 200 dissolved oxygen meter (E-004-28) YSI pH meter (E-023-20) HACH 2100P Turbidimeter (E-047-1)

Date (Weather)	Location	Time	Water Depth (m)	Water Temp. (°C)	DO level (mg/L)	DOS (%)	Turbidity (NTU)	pH (unit)	SS (mg/L)	Remarks and Observation
12/11/2009 (Cloudy)	W2	11:12	0.80	25.5	8.54	107.5	3.21	8.45	<1	Excavation
	W3	10:53	0.30	26.5	7.11	91.9	23.9	7.93	21	
	W5	10:28	0.25	26.2	6.42	82.2	7.75	7.86	<1	-
	W7	10:04	1.20	25.6	5.12	67.8	4.57	7.69	3	

Prepared by :S.N. Kong	Certified by :
	Date : 30 (w (w)7
The copyright of this document is owned by Fugro Technical Services Limited. It may no	t be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

MateriaLab

Our Ref. No.: 075117WA91895

 Client
 : Sum Kee Construction Limited

 Project
 : DC/2006/01 Drainage Improvement Works in Sai Kung

Impact Water Quality Monitoring Field Data Record

Equipment : YSI model DO 200 dissolved oxygen meter (E-004-28) YSI pH meter (E-023-20) HACH 2100P Turbidimeter (E-047-1)

Date (Weather)	Location	Time	Water Depth (m)	Water Temp. (°C)	DO level (mg/L)	DOS (%)	Turbidity (NTU)	pH (unit)	SS (mg/L)	Remarks and Observation
17/11/2009 (Cloudy)	W2	11:33	0.90	17.3	9.94	103.4	3.82	8.97	2	-
	W3	11:18	0.60	18.6	8.16	87.6	46.3	7.90	39	-
	W5	10:54	0.51	20.8	7.31	81.7	3.21	7.66	2	-
	W7	10:38	1.54	17.9	7.73	81.5	4.46	8.12	8	° _

Prepared by : S.N. Kong

Certified by : Approved Signatory: K.F. Wong Date

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233 Fax : +852-2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk

MateriaLab

Our Ref. No.: 075117WA91895

Client : Sum Kee Construction Limited Project

: DC/2006/01 Drainage Improvement Works in Sai Kung

Impact Water Quality Monitoring Field Data Record

Equipment : YSI model DO 200 dissolved oxygen meter (E-004-28) YSI pH meter (E-023-20) HACH 2100P Turbidimeter (E-047-1)

Date (Weather)	Location	Time	Water Depth (m)	Water Temp. (°C)	DO level (mg/L)	DOS (%)	Turbidity (NTU)	pH (unit)	SS (mg/L)	Remarks and Observation
19/11/2009 (Fine)	W2	11:26	0.90	18.3	9.07	96.2	2.34	8.76	<1	-
	W3	11:09	0.48	19.6	7.63	82.6	14.5	7.79	14	-
	W5	10:48	0.53	20.1	8.28	91.5	3.55	7.66	4	-
	W7	10:33	1.26	19.8	8.17	89.9	3.68	7.62	4	-

Prepared by : <u>S.N. Kong</u>

Certified by : Approved Signatory: K.F. Wong

Date

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233 Fax : +852-2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk

MateriaLab

Our Ref. No.: 075117WA91895

Client

: Sum Kee Construction Limited

Project : DC/2006/01 Drainage Improvement Works in Sai Kung

Impact Water Quality Monitoring Field Data Record

Equipment : YSI model DO 200 dissolved oxygen meter (E-004-28) YSI pH meter (E-023-20) HACH 2100P Turbidimeter (E-047-1)

Date (Weather)	Location	Time	Water Depth (m)	Water Temp. (°C)	DO level (mg/L)	DOS (%)	Turbidity (NTU)	pH (unit)	SS (mg/L)	Remarks and Observation
24/11/2009 (Fine)	W2	11:15	0.85	22.8	9.75	112.6	2.83	9.03	<1	-
	W3	10:58	0.10	26.6	7.35	91.6	36.7	7.85	32	-
	W5	10:41	0.05	22.5	7.50	86.4	2.82	7.99	2	-
	W7	10:20	1.20	23.2	6.42	74.9	5.12	7.79	5	-

Prepared by : _____S.N. Kong

Certified by : Approved Signatory: K.F. Wong

Date

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233 Fax : +852-2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk

MateriaLab

Our Ref. No.: 075117WA91895

Client : Sum Kee Construction Limited

Project : DC/2006/01 Drainage Improvement Works in Sai Kung

Impact Water Quality Monitoring Field Data Record

Equipment : YSI model DO 200 dissolved oxygen meter (E-004-28) YSI pH meter (E-023-20) HACH 2100P Turbidimeter (E-047-1)

Date (Weather)	Location	Time	Water Depth (m)	Water Temp. (°C)	DO level (mg/L)	DOS (%)	Turbidity (NTU)	pH (unit)	SS (mg/L)	Remarks and Observation
26/11/2009 (Cloudy)	W2	11:02	0.85	23.0	8.48	98.4	4.37	9.04	3	
	W3	10:41	0.08	24.8	7.87	95.1	20.7	7.68	18	· _
	W5	10:18	0.05	23.6	6.92	81.6	2.61	7.53	3	· · · · _
	W7	10:02	1.23	24.0	5.87	70.4	4.75	7.55	4	-

Prepared by : S.N. Kong

Certified by : Approved Signatory: K.F. Wong

Date

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

Tel : +852-2450 8233 Fax : +852-2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk

MateriaLab

Ref. No. : 075117EN90614

Client : Sum Kee Construction Limited Project : Contract No. DC/2006/05 Drainage Improvement Works in Sai Kung

Impact Daytime Noise Level Monitoring Results

Location	HCM1 - In fr	ont of door	No. 5B, 1st Lane at Ho Chung Villa	age		
Date	Sampling Time	Weather Condition	Site Condition	Wind speed (m/s)	LA	_{eq} dB(A)
					L ₁₀	58.5
05/11/2009	14:49-15:19	Fine	Trench Work	<1	L ₉₀	47.0
					Leq	56.1
					L ₁₀	58.0
12/11/2009	13:00-13:30	Cloudy	Excavation	<1	L ₉₀	45.0
					Leq	55.7
					L ₁₀	64.0
19/11/2009	14:25-14:55	Fine	Trench Work	<1	L ₉₀	52.5
					Leq	60.5
					L ₁₀	61.0
26/11/2009	14:32-15:02	Cloudy	Trench Work	<1	L ₉₀	51.5
					Leq	57.6

Prepared by : _____ S.N. Kong

Certified by : Approved Signatory: K Date :

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.
 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

MateriaLab

Ref. No. : 075117EN90614

Client : Sum Kee Construction Limited

Project : Contract No. DC/2006/05 Drainage Improvement Works in Sai Kung

Location	HCM2 - In front of door No. 107 at Ho Chung New Village					
Date	Sampling Time	Weather Condition	Site Condition	Wind speed (m/s)	LA _{eq} dB(A)	
					L ₁₀	59.5
05/11/2009	14:09-14:39	Fine	Trench Work	<1	L ₉₀	46.0
					Leq	55.9
12/11/2009	13:34-14:04	Cloudy			L ₁₀	68.5
			Excavation	<1	L ₉₀	47.0
					Leq	63.1
					L ₁₀	54.5
19/11/2009	13:46-14:16	Fine	Trench Work	1-2	L ₉₀	45.5
					Leq	51.4
26/11/2009	13:51-14:21	Cloudy	Trench Work	<1	L ₁₀	64.0
					L ₉₀	46.0
					Leq	60.2

Impact Daytime Noise Level Monitoring Results

Prepared by : S.N. Kong

Certif

Certified by : Approved Signatory: K.F. Wong 12 wo 50 Date :

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong. Tel : +852-2450 8233 Fax : +852-2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk

MateriaLab

Ref. No. : 075117EN90614

Client : Sum Kee Construction Limited

Project : Contract No. DC/2006/05 Drainage Improvement Works in Sai Kung

Impact Daytime Noise Level Monitoring Results

Location	PKM1 - At the side of door No. 14 at Fung On Village, Tai Chung Hau					
Date	Sampling Time	Weather Condition	Site Condition	Wind speed (m/s)	LA _{eq} dB(A)	
					L ₁₀	54.5
03/11/2009	14:14-14:44	Fine	No Special Site Activity	<1	L ₉₀	48.0
					Leq	52.8
	14:14-14:44	Fine	No Special Site Activity	<1	L ₁₀	64.0
10/11/2009					L ₉₀	48.5
a 1					Leq	59.1
					L ₁₀	56.5
17/11/2009	16:00-16:30	Cloudy	No Special Site Activity	1-2	L ₉₀	49.0
					Leq	54.4
					L ₁₀	56.5
24/11/2009	15:41-16:11	Fine	No Special Site Activity	<1	L ₉₀	48.0
					Leq	54.4

Prepared by : S.N. Kong

Certified by :

Approved Signatory: K.F. Wong Balin mo Date :

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

: +852-2450 8233 : +852-2450 6138 E-mail : matlab@fugro.com.hk Website : www.materialab.com.hk

MateriaLab

Ref. No. : 075117EN90614

Client : Sum Kee Construction Limited

Project : Contract No. DC/2006/05 Drainage Improvement Works in Sai Kung

Location	PKM2 - In front of Green House Nursery at Pak Kong Riverside					
Date	Sampling Time	Weather Condition	Site Condition	Wind speed (m/s)	LA _{eq} dB(A)	
					L ₁₀	60.5
03/11/2009	13:39-14:09	Fine	No Special Site Activities	1-2	L ₉₀	50.5
					Leq	57.7
	14:48-15:18	Fine	No Special Site Activities	<1	L ₁₀	63.0
10/11/2009					L ₉₀	53.0
					Leq	61.2
					L ₁₀	62.0
17/11/2009	15:22-15:52	Cloudy	No Special Site Activities	1-2	L ₉₀	52.0
					Leq	59.6
					L ₁₀	62.5
24/11/2009	15:06-15:36	Fine	No Special Site Activities	<1	L ₉₀	52.5
					Leq	60.9

Impact Daytime Noise Level Monitoring Results

Prepared by : S.N. Kong

Certified by : Approved Signatory: K.F. Wong Date :

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

MateriaLab

Ref. No. : 075117EN90614

Client : Sum Kee Construction Limited

Project : Contract No. DC/2006/05 Drainage Improvement Works in Sai Kung

Impact Daytime Noise Level Monitoring Results

Location	cation SKM1 - In front of door No. 13 at Muk Min Shan					
Date	Sampling Time	Weather Condition	Site Condition	Wind speed (m/s)	LA _{eq} dB(A)	
					L ₁₀	57.5
03/11/2009	15:35-16:05	Fine	Excavation	<1	L ₉₀	47.0
	5				Leq	55.3
10/11/2009	13:00-13:30	Fine	Excavation	1-2	L ₁₀	58.5
					L ₉₀ -	48.0
					Leq	55.6
					L ₁₀	60.0
17/11/2009	14:36-15:06	Cloudy	Planting	2-3	L ₉₀	50.0
					Leq	57.8
					L ₁₀	56.0
24/11/2009	14:23-14:53	Fine	No Special Site Activities	<1	L ₉₀	46.5
					Leq	53.6

Prepared by : S.N. Kong

Certified by : Approved Signatory: K.F. Wond Date :

The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

MateriaLab Division, Fugro Development Centre, 5 Lok Yi Street, 17 M.S. Castle Peak Road, Tai Lam, Tuen Mun, N.T., Hong Kong.

 Tel
 : +852-2450 8233

 Fax
 : +852-2450 6138

 E-mail
 : matlab@fugro.com.hk

 Website
 : www.materialab.com.hk

MateriaLab

Ref. No. : 075117EN90614

Client : Sum Kee Construction Limited

Project : Contract No. DC/2006/05 Drainage Improvement Works in Sai Kung

Impact Daytime Noise Level Monitoring Results

Location	SKM2 - In front of Waste Recycling Site at Muk Min Shan					
Date	Sampling Time	Weather Condition	Site Condition	Wind speed (m/s)	LA _{eq} dB(A)	
			5		L ₁₀	65.0
03/11/2009	15:01-15:31	Fine	Excavation	<1	L ₉₀	53.0
					Leq	66.3
10/11/2009	13:34-14:04	Fine	Excavation	<1	L ₁₀	68.0
					L ₉₀	56.5
					Leq	66.7
	14:03-14:33	Cloudy	Planting	1-2	L ₁₀	66.5
17/11/2009					L ₉₀	54.5
					Leq	66.8
24/11/2009	13:50-14:20) Fine	No Special Site Activities	<1	L ₁₀	61.0
					L ₉₀	48.0
					Leq	58.0

Prepared by : S.N. Kong

Certified by :


Approved Signatory: K.F. Wong Date :


The copyright of this document is owned by Fugro Technical Services Limited. It may not be reproduced except with prior written approval from the Company.

Appendix 5

Graphical Presentation of Water and Noise Monitoring Data


DO Level at Ho Chung River

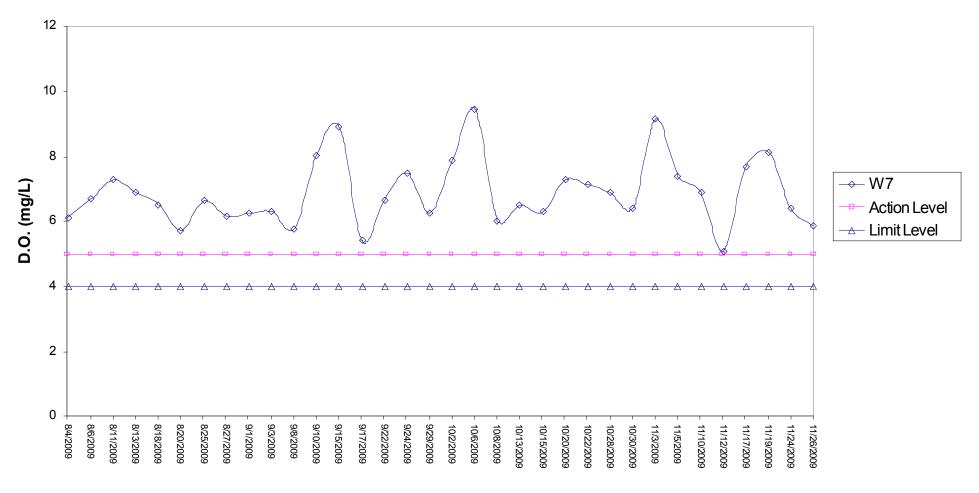

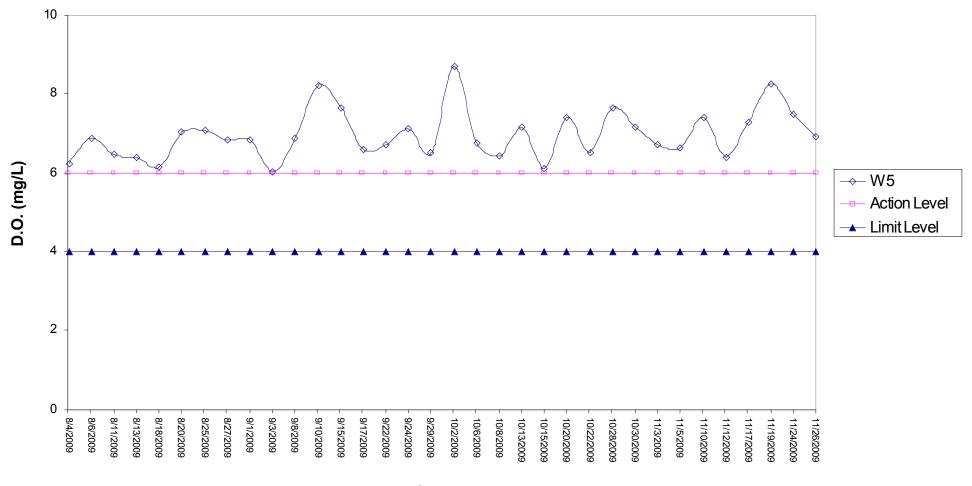


DO Level at Pak Kong River


DO Level at Sai Kung River

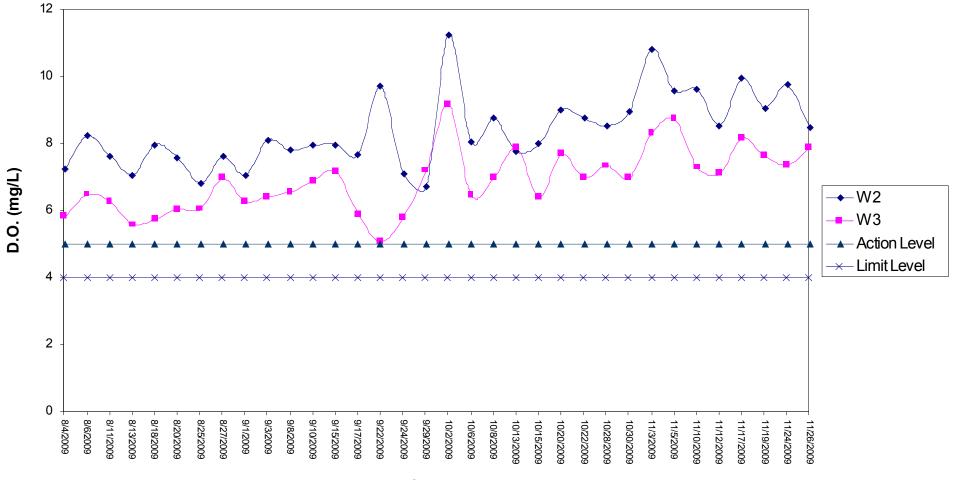


Turbidity Level at Ho Chung River

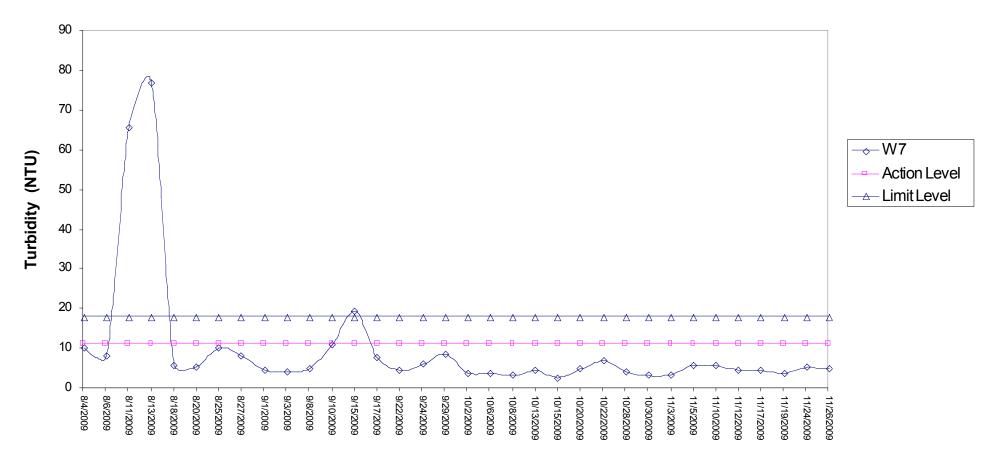


Turbidity Level at Pak Kong River

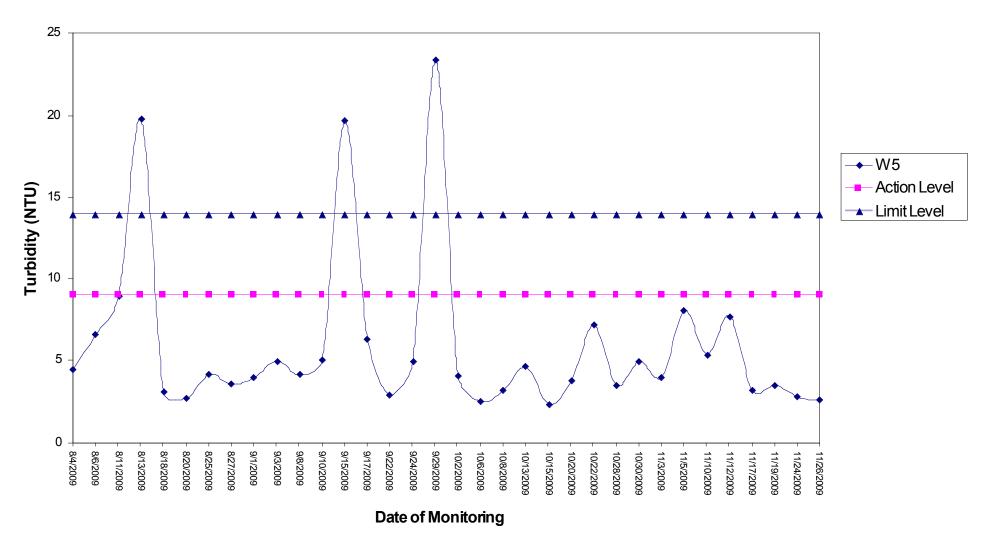




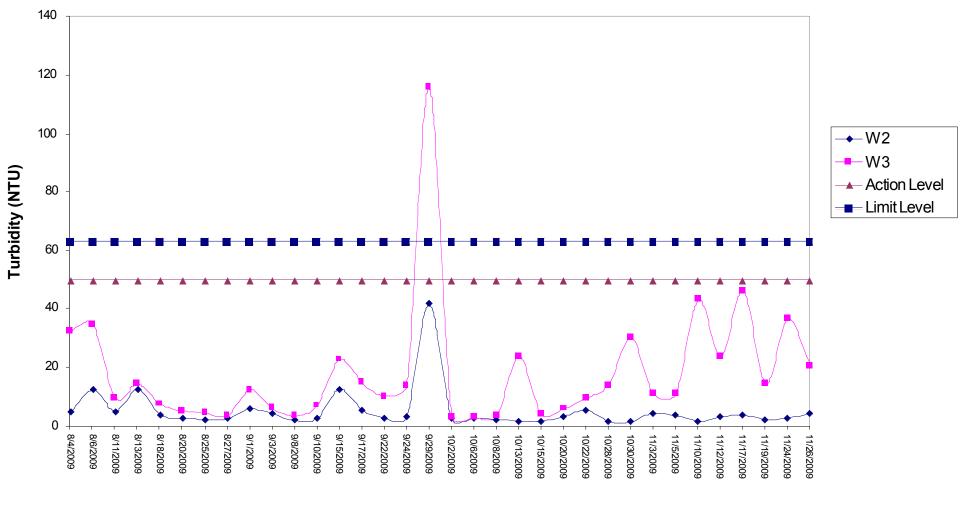


SS content at Ho Chung River

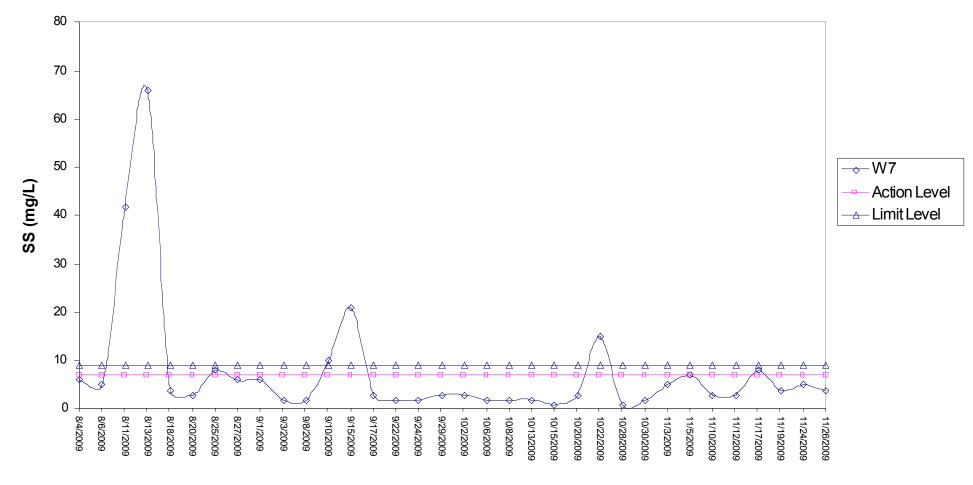




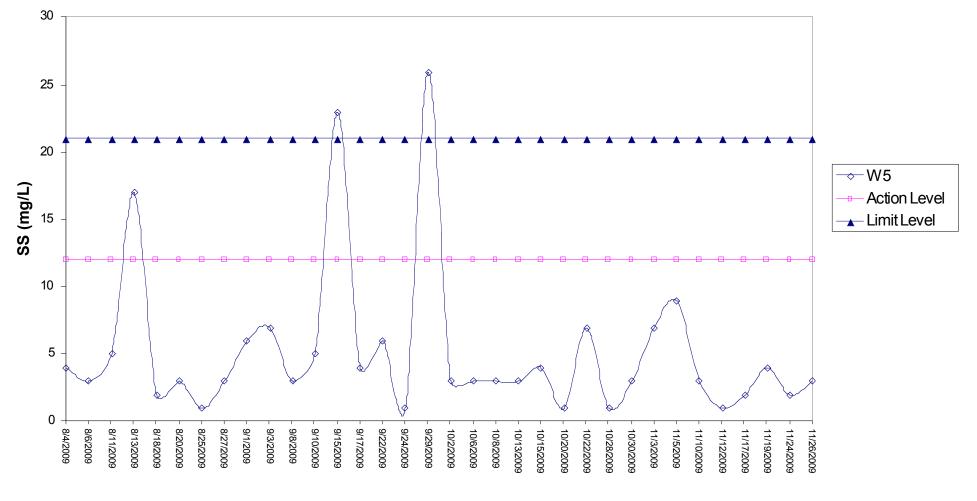


SS content at Sai Kung River

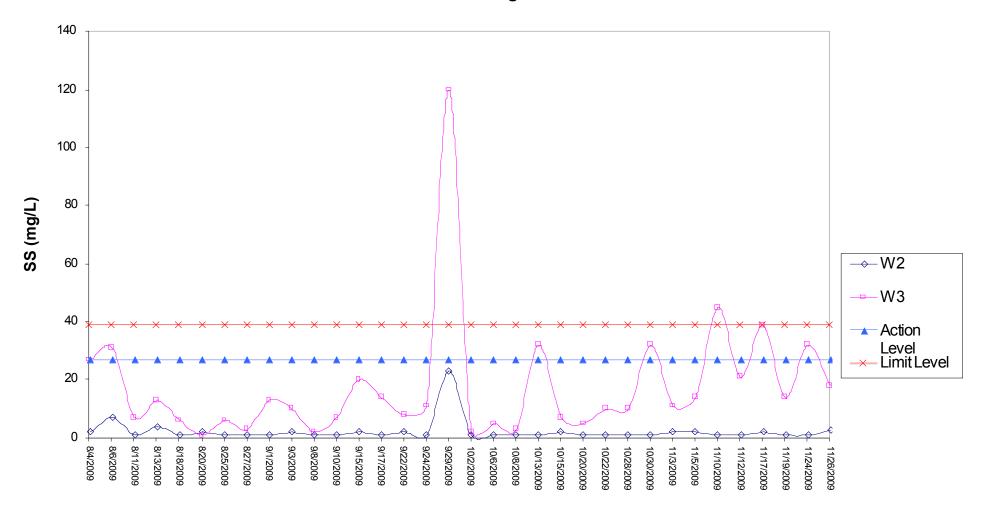

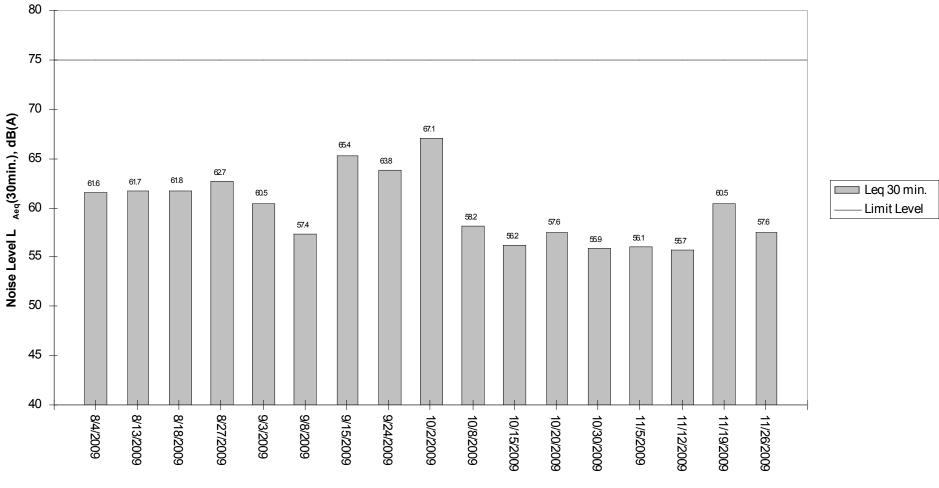


Daytime Noise Level Monitoring at HCM1

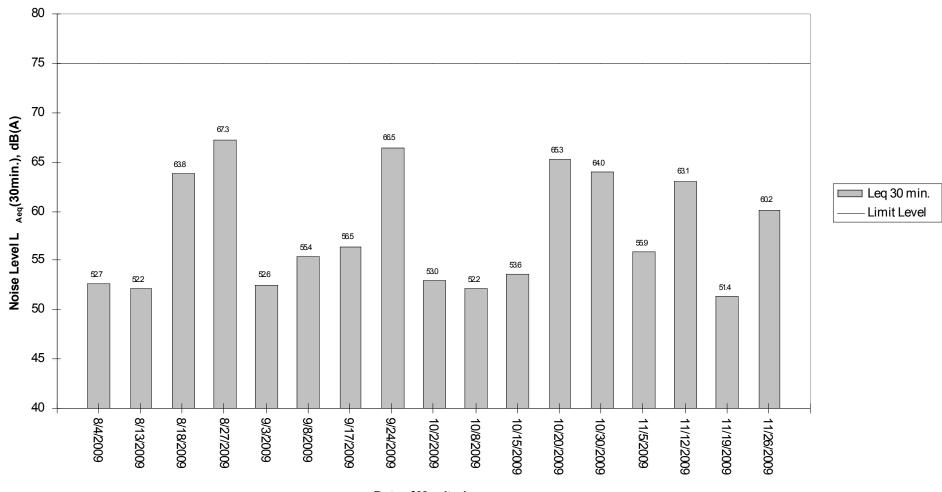


Daytime Noise Level Monitoring at HCM2


Date of Monitoring



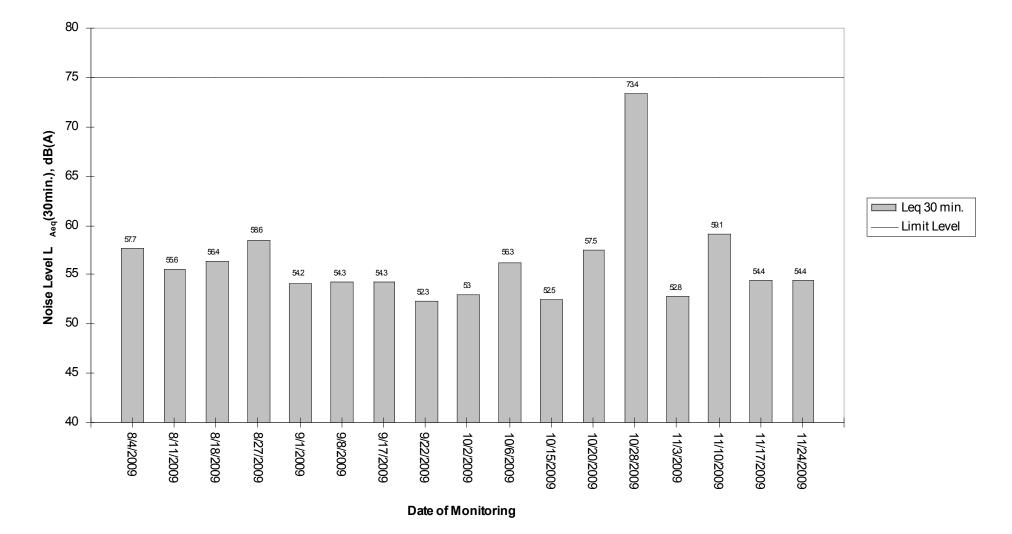

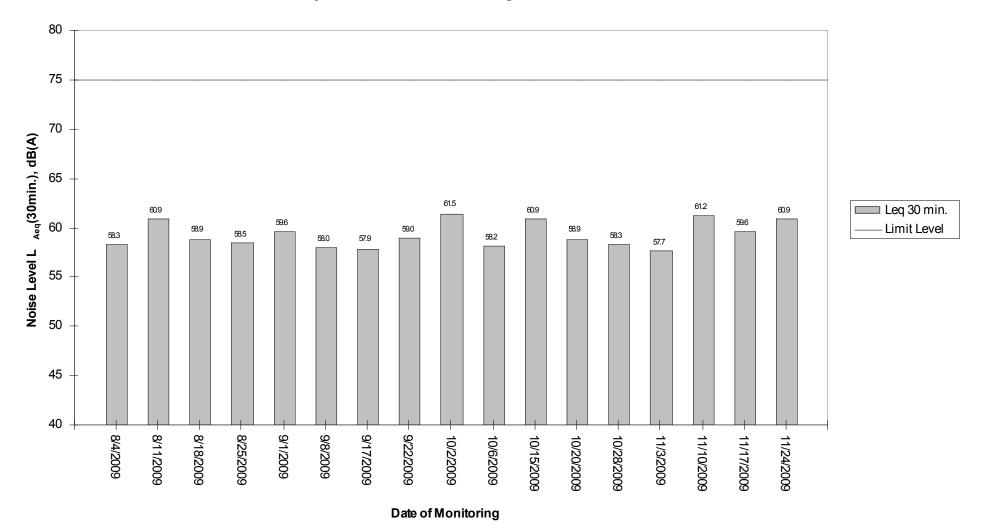


Daytime Noise Level Monitoring at PKM2

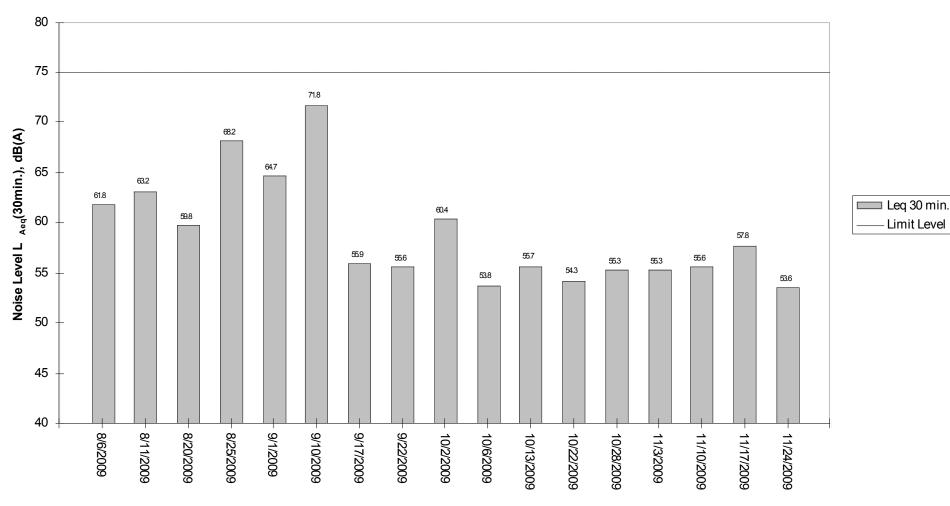

Daytime Noise Level Monitoring at SKM1

Date of Monitoring

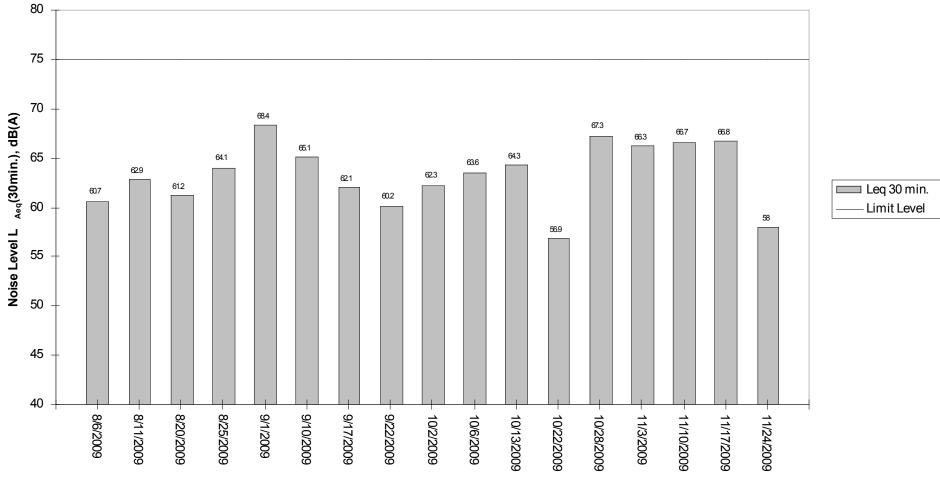

Daytime Noise Level Monitoring at SKM2

Date of Monitoring

Event Action Plan for Air, Noise and Water Monitoring

Event/ Action Plan for Air Quality

EVENT		ACTION		
EVENI	ET	IC(E)	ER	CONTRACTOR
ACTION LEVEL				
1. Receipt of complaint related to construction dust	 Identify source, investigate the causes of complaints and propose remedial measures; Inform IC(E) and ER; Conduct <i>ad hoc</i> monitoring to confirm finding; Carrying out investigation to identify the source /reasons of complaints. Investigation shall be completed within 1 weeks; Rectify any unacceptable practice; Amended working methods if required; Correspond to the complainant within 10 days to inform the cause of the nuisance and action taken. 	 Supervise Investigation process; Check monitoring data submitted by ET; Check Contractor's working method. 	1. Notify Contractor.	 Rectify any unacceptable practice; Assist ET to find the root cause of the complaint; Amend working methods if appropriate.
		1.0.		1 77 1 1 1
1. Exceedance for two <i>ad hoc</i> monitoring sample or more complaints in 3 months	 Identify source, investigate the causes of exceedance/complaints and propose remedial measures; Inform ER, Contractor and EPD; Repeat measurement to confirm finding; Carrying out investigation to identify the source /reasons of complaints. Investigation shall be completed within 1 weeks; Correspond to the complainant within 10 days to inform the cause of the nuisance and action taken; Increase monitoring frequency to daily; Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results; If exceedance stops, cease <i>ad hoc</i> monitoring. 	 Supervise Investigation process; Check monitoring data submitted by ET; Check Contractor's working method; Discuss with ET and Contractor on possible remedial measures; Advise the ER on the effectiveness of the proposed remedial measures; Supervise implementation of remedial measures. 	 Confirm receipt of notification of failure in writing; Notify Contractor; Ensure remedial measures properly implemented; If exceedance continues, consider what portion of the work is responsible and instruct the contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance; Submit proposals for remedial actions to IC(E) within 3 working days of notification; Implement the agreed proposals; Amend proposal if appropriate; Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event/Action Plan for Construction Noise

EVENT	ET	ACTION IC(E)	ER	CONTRACTOR
ACTION LEVEL				
	 Undertake measurement to establish validity of complaint. Identify the source(s) of the complaint. Inform ER & IC(E) in writing. Discuss remedial actions required with ER & IC(E). Increase monitoring frequency to assess efficacy of remedial measures. If exceedance continues, meet with ER&IC(E) to review implementation of appropriate mitigation measures. If exceedance stops, cease additional monitoring. 	 Review the analyzed results submitted by the ET. Review the proposed remedial measures by the Contractor and advise the ER & ET accordingly. Supervise the implementation of remedial measures. 	 Confirm receipt of notification of complaint and notify Contractor if proven. Check monitoring data trends and Contractor's working methods. Remind the Contractor of his contractual obligations and discuss with ET, IC(E) and Contractor on proposed remedial actions. Assess the efficacy of remedial actions and keep the Contractor informed. Inform complainant of actions taken. 	 Submit proposals for remedial actions to ER within three working days of notification. Amend proposals if required by the Engineer. Implement the remedial actions immediately upon instruction. Liaise with the ER to optimise the effectiveness of the agreed mitigation. Amend proposals if appropriate.
	 Repeat measurement to confirm findings. Identify the source(s) of impact. Inform ER, IC(E) and EPD in writing. Discuss remedial actions required with ER & IC(E). Increase monitoring frequency to assess efficacy of remedial measures. If exceedance continues, meet with ER&IC(E) to identify appropriate mitigation measures. If exceedance stops, cease additional monitoring. 	 Check monitoring data submitted by the ET. Review Contractor's remedial actions to assure their effectiveness and advise the ER & ET accordingly. Supervise the implementation of remedial measures. 	 Confirm receipt of notification of exceedance and notify Contractor. Check monitoring data trends and Contractor's working methods. Discuss with ET, IC(E) and Contractor on proposed remedial actions to be implemented. Assess the efficacy of remedial actions and keep the Contractor informed. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	 Take immediate action to avoid further exceedance. Submit proposals for remedial actions to ER within three working days of notification. Amend proposals if required by the ER. Implement the remedial actions immediately upon instruction. Liaise with the ER to optimise the effectiveness of the agreed mitigation. Resubmit proposals if problem still not under control. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Event/Action Plan for Water Quality Monitoring

EVENT		ACTION		
ACTION LEVEL	ET	IC(E)	ER	CONTRACTOR
Action Level being exceeded by one sampling day	 Repeat in-situ measurement to confirm findings; Identify reasons for non- compliance and sources of impact; Inform IC(E) and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IC(E) and Contractor; Repeat measurement on next day of exceedance. 	 Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. 	 Discuss with IC(E) on the proposed mitigation measures; make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. 	 Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER; Implement the agreed mitigation measures.
LIMIT LEVEL Action Level being exceeded by more than two consecutive sampling days	 Repeat in-situ measurement to confirm findings; Identify reasons for non- compliance and sources of impact; Inform IC(E) and Contractor; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IC(E) and Contractor; Ensure mitigation measures are implemented; Prepare to increase the monitoring frequency to daily; Repeat measurement on next day of exceedance. 	 Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. 	 Discuss with IC(E) on the proposed mitigation measures; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. 	 Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET and IC(E) and propose mitigation measures to IC(E) and ER within 3 working days; Implement the agreed mitigation measures.

Event/Action Plan for Water Quality Monitoring(continued)

EVENT		ACTION		
	ET	IC(E)	ER	CONTRACTOR
Limit Level being exceeded by one sampling day	 Repeat in-situ measurement to confirm findings; Identify reasons for non- compliance and sources of impact; Inform IC(E), Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IC(E), ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit Level. 	 Discuss with ET and Contractor on the mitigation measures; Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; Assess the effectiveness of the implemented mitigation measures. 	 Discuss with IC(E), ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures. 	 Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IC(E) and ER and propose mitigation measures to IC(E) and ER within 3 working days; Implement the agreed mitigation measures.
LIMIT LEVEL Limit Level being exceeded by more than two consecutive sampling days	 Repeat in-situ measurement to confirm findings; Identify reasons for non- compliance and sources of impact; Inform IC(E), Contractor and EPD; Check monitoring data, all plant, equipment and Contractor's working methods; Discuss mitigation measures with IC(E), ER and Contractor; Ensure mitigation measures are implemented; Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days. 	1. Discuss with ET and Contractor on the mitigation measures; 2. Review proposals on mitigation measures submitted by Contractor and advise the ER accordingly; 3. Assess the effectiveness of the implemented mitigation measures.	 Discuss with IC(E), ET and Contractor on the proposed mitigation measures; Request Contractor to critically review the working methods; Make agreement on the mitigation measures to be implemented; Assess the effectiveness of the implemented mitigation measures; Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the marine work until no exceedance of Limit Level. 	 Inform the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; Check all plant and equipment; Consider changes of working methods; Discuss with ET, IC(E) and ER and propose mitigation measures to IC(E) and ER within 3 working days; Implement the agreed mitigation measures; As directed by the ER, to slow down or to stop all or part of the marine work or construction activities.

Equipment Details

Dust Monitoring Equipment

EQUIPMENT LIST	MODEL	CALIBRATION FREQUENCY
 High volume sampler with flow controller, including : motor/blower assembly filter holder G901 ET1 Elapsed time indicator G310 Flow controller G105 Flow recorder with cartridge and charts G70 Seven-day mechanical timer Aluminum shelter 	GMW SA2310-105	One point calibration : every 600 hours of sampling or after replacement of motor/motor brushes
Variable Resistance Calibrator Orifice	Andersen G3357K S/N : 42J/74N	Annually
Anemometer	Hishimatsu TN-24	-


Noise Monitoring Equipment


EQUIPMENT LIST	MODEL	CALIBRATION FREQUENCY
Precision integrating sound level meter	B&K 2236 B&K 2238	Annually
Sound level calibrator	B&K 4230 B&K 4231	Annually
Microphone extension cable (3m)	B&K A00027 B&K A00185 B&K A00408	-
Portable Combination Anemometer	-	-


Water Monitoring Equipment


EQUIPMENT LIST	MODEL	CALIBRATION FREQUENCY
Turbidity meter	HACH 2100P	3 months
Dissolved oxygen meter	YSI DO 200 with stirrer	3 months
Thermometer	Standard calibrated thermometer	6 months
PH meter	Hanna HI9024	3 months


Figure

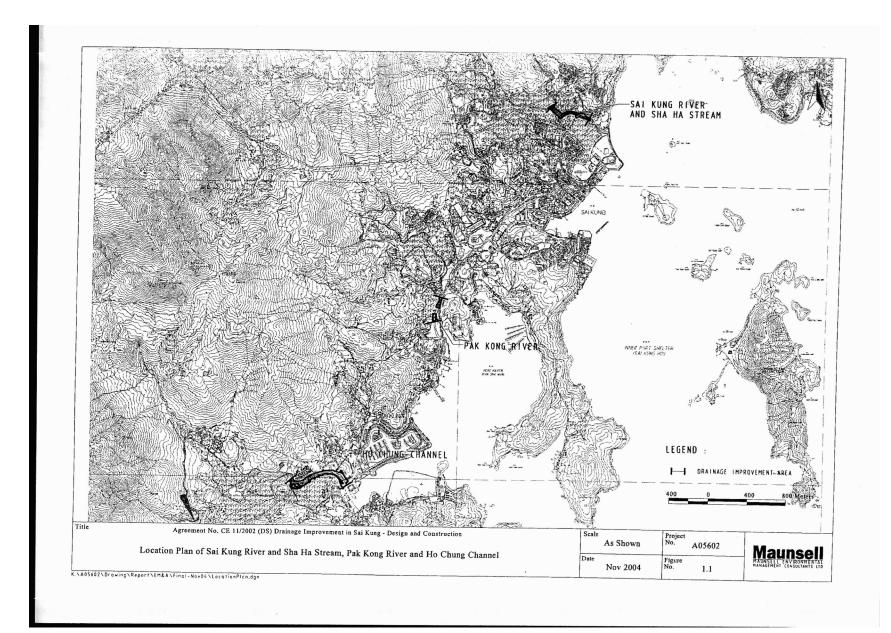

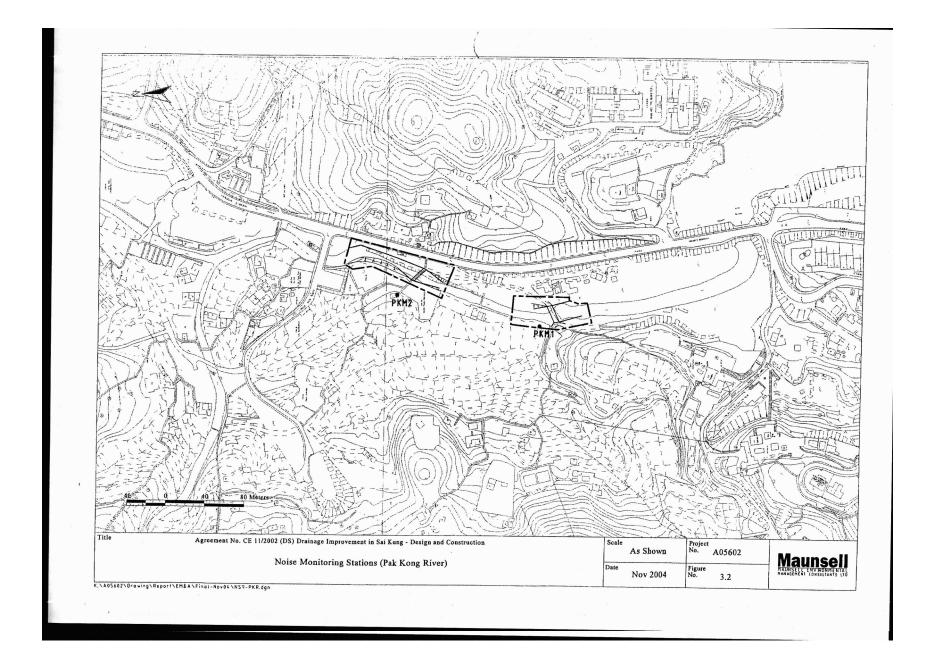

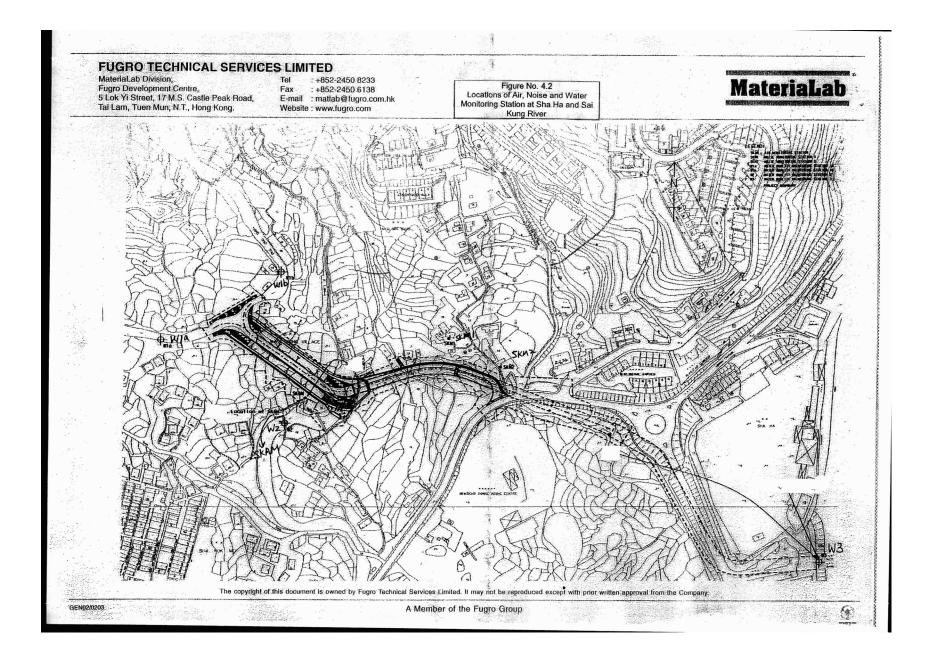

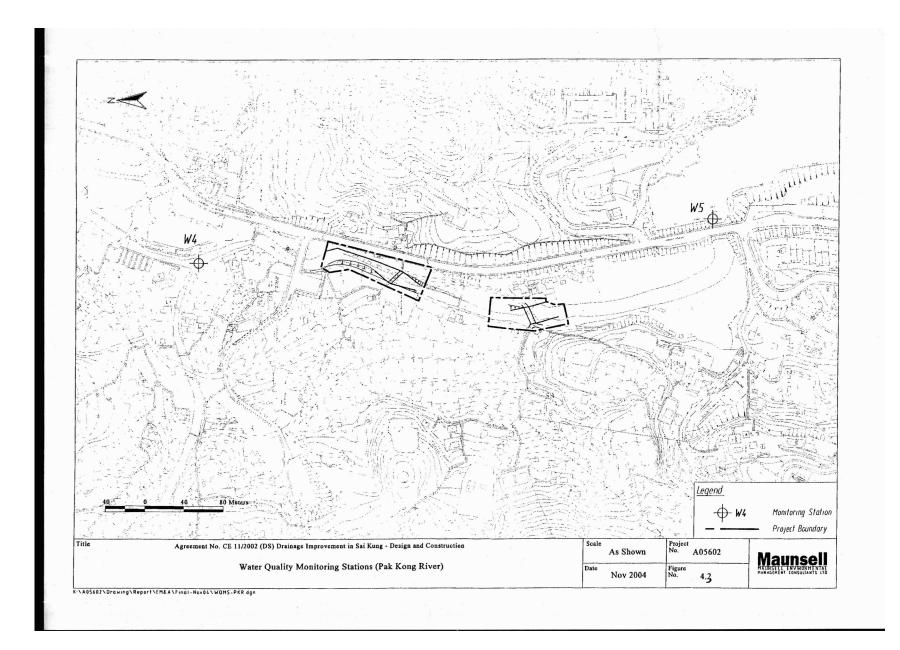


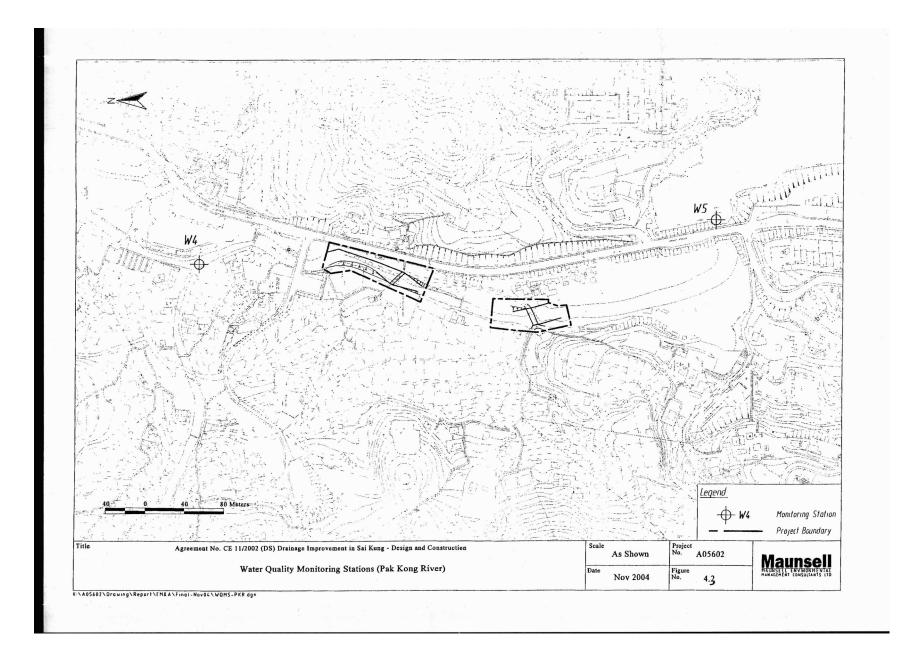

Work Programme

`

	Contract No. DC/2006/01 - Drainage Improvement Works in Sai Kung																
5 11	4 Name	Distation	Start	Frieb Productions			Master Prog			- 1							
1	ndruct Key Dates	1215 days		10/7/26	Nov Der	Jan Reb Mar Apr 1	Nov Jun Jui Aug Sep	Od Nev Dec In	n Feb Mar Are Mar Jun Jul	Ang Sep Oct Nov Dec J	en Reb Alar Apr Abr	y Jun Jul Ang S	p Oci Nov Dec	Lo lich Mar .	Apr May Jun Mil	Aug Sep 1001	No. Dec. Mr.
	Commencement of the Works	fl days	07 3 30	07:3/30		÷ 3/30					t		i	F			(a)
-	Completion of Section 1 of the Works Completion of Section II of the Works	0 days 0 days	11973-29 1197-26	09 3 29 2FS+731 days 09 7 26 2FS+850 days	a 1. a 1.						\$-3/8-	-					
5	Completion of Section III of the Works	0 days	08 11 2 .	08-11-2 2FS+584 days						-H2-	1.		1.8				
-	Completion of Section IV of the Works Completion of Section V of the Works	0 days 0 days	09 7 26 10 3 29	09/7/26/2F8+850 days 10/3/29/2F8+1096 days						anna a ann an A				1	-1/29		
8	Completion of Section VI of the Works	9 days	10 7 26	10 7 26 2F8+1215 days	· · · · · ·					1000			1		-327	-7/26	
O E	Completion of Section VII of the Works tended Completion Dates	0 days	09112	199 11-2 21% (949 days									11/2				
	Completion of Section 1 of the Works	a spàra	09 5 22	09.3.22 3PS (54 days	in a promotion					e		5/22			the second second	and the second	
3	Completion of Section II of the Works Completion of Section III of the Works	9 days 0 days	09919	1919-19-4F8+54,5 days 08-12-23-5F8+50-5 days						1 ,	202		• 9/19				1000
×	Completion of Section IV of the Works Completion of Section V of the Works	0 days	69 9 19	09.9-19 GFS+54.5 days							20	1	♦ 9/19		1	a null	
10	Completion of Section VI of the Works	0 days 0 days	10.5.11 10.97	10.5.11 7FS+42.5 days 10.9.7 8FS+42.5 days	e to closed				l pre a secondaria						♦ \$/11	• an	
	Completion of Section VII of the Works section of Site	0 days 195 days	09 12 15	09 12 15 9FS+42.5 days			in the second second						÷ 12	V15		•	
0	Portion A1	0 days	07 3 30	07 3 30		♦ 3/30		-									
59	Portion A2 Portion B1	0 days 0 days	07 7 12	07 7 12 07 3 30	an and a succession		7/12										
2	Portion B2	0 days	07 7-12	07712		\$ 3/30	♦ 7/12										
3	Portion 113 Portion C1	0 Jays 0 days	07/10/11	67/10/11 07/3/30	Same and		83 handed over on 18 Oct 07	 1011 									S
<	Portion C2	II days	17712	07.7 12		3/30	♦ 7/12										
1	Portion C3 Portion C4	ti days U days	07.4.26 07.10.11	07.4.26 07.10.11		٠	4/26										
x ·	Portion CS	0 days	07 3 30	07.1.30	ist com	\$ 3/30		10/11									
2	Pentien D Pentien F	0 days 0 days	07.3.30	07.3 to 07.4.11		 3/30 4/1 											
	climinary works	244 days	17/3/29	67/11/27		• 41											
0	Handover of Portnons D & E Portnone D & E site clearance + Initial Survey	13 days 13 days	07.3.30 07.3.30	07 4 11 67 4 11 32		17											
и	Prepare site offices layout for approval	35 days	417 3.301	07.5.3 32			1										
6	Exection of Contractor's site office Exection of FR's site office	34 days 87 days	07 4 12 07 4 3	07315 3433			*) 		a and an in the second								an ann an
	Collect existing records from FT's	41 days	17 1 29	07.5 x		1	h										
8	Coordination with Villagest Environmental Baseline Mondorine	111 days 58 days	07.3 hu 07.5.3	07 7 18 07 6 29 38			1										
8	Condition Succey Proposal	.35 days	07 5 N	07-611 38		6											No. of Lot of Lo
3	Submission under Environmental Permit Controncement Date Notification (Item 1.11)	191 days 52 days	07/5/21	07/11/27 07.7.11			J.	and the second second									
1	Detailed Fish Ladder Design (Item 3.1)	96 days	07 5 28	07831	1.000												
-	Stream Design Proposal (Item 3-2) Dehaled Transplantation Proposal for Effectiv acumenta (Item 3-4)	t day 166 days	07.6-4	07.6-4 117.11.27				promotion									1.1
6 Se	Resetine Monitoring Report (New 4.3) tion 1	4 days	07/6/30	0773			I Channed		· · · · · · · · · · · · · · · · · · ·								1000
S Se	tion I Works in Portion II at Sha Ha	885 days 885 days	07/3/30	0%%/30 0%%/30													×
0	Preliminary work at Portion B1 Nandover of Portion B1	195 days	07/3/30 07:3-30	87/ja/ja 67.3/30				-									
1	Coordination with Villagers	0 days 85 days	07.3-30 07.3-30	- 67.3/30 07.6/22 \$0		♦ _1/30		uff anna Sa	oo ar areas asanaasaayaa	nun anananananan			aansaaaaad			, manananan	inen ende
1	Site elemence (Initial Survey) Utilities Detection	311 clay x	07:3:30	117-1-28 5n		. D.											
	Erection of Hearding	43 days 30 days	07:5.9 07:6.30	0762037.52 0772953,39,40													
	Preparation for G1 works NP Appleciation (for G1)	30 days 150 days	07 3 30 07 4 22	07.428 50 07.925 55													
	G1 & Instrument Installation	15 days	67.9.26	07 10 10 56		14											
	Trees Survey & Reporting RF: Comments on Tree Survey Report	17 days 14 days	07 4 29 07 5 16	07.5.15.32 07.5.29.58		Ľ	4										
-	Transplanting	14 days 90 days	07 5 16	07/9/20 51,59			FT										
	Preliminary work at Portion B2 Handover of Portion B2	106 days 0 days	07/7/12 107/7 12	07/10/25						1							
	Site clearance + Initial Survey	30 days	17713	07:8:11 62			* 7/12										
	Vilities Detection Exection of Hearding	30 days 30 days	67 7 28 67 8 17	07.8:26 63FS-15 days 07.9:15 64FS-10 days,54													
	G.I. & Instrument Installation	15 days	07 9 26	07 10 10 64								i ana ana ana ana ana ana ana ana ana an					
	Demolech existing structures Trees Survey & Reporting	40 days 5 days		07/10/25 65 07/7 17 62			↓ Ĕ	Th									
1	RE Commonis on Tree Survey Report	10 days	07 7 18	07/7/27 68				LINE CONTRACTOR									1.00
	Trees Felling Transplanting	10 days 90 days	07 7 28	07%6 69 07.10.25 69			Į į	in the second se									
2	Preliminary work at Portion B3	74 days	07/10/11	07/12/23													
	Handover of Portion B3 Situ clearance - Initial Survey	0 days	07/10/11 07/10/11	97/10/11 07/11/2 73				•									
-	Site charance + Initial Survey Utilities Detection	23 days 30 days	07/10/11	07.11.2 73 07.12.2 74				Hen									
ision (e: 19 N							<u></u>	(1102:00)									i

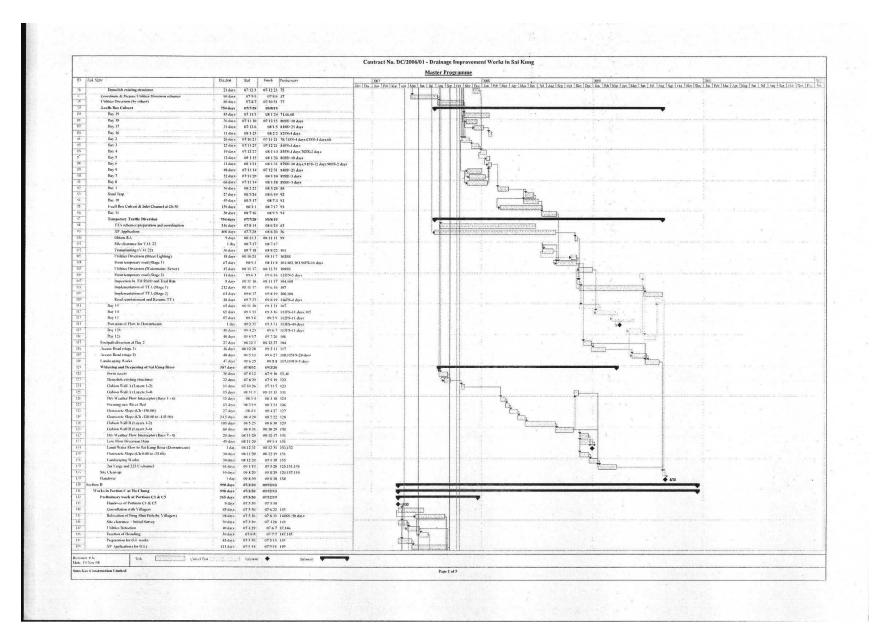

meen brokhanne wek 1 Parkinn (3 4 Penine (2 4 Penine (103 days 07 0 days 07 30 days 07 40 days 07 161 days 07 30 days 07 30 days 07 30 days 07 16 days 07 16 days 07 16 days 07 16 days 07 17 days 07 18 days 07 90 days 17 18 days 07 19 days 17	(39) (37)/30 (37) (37)/31 (37) (37)/31 (37) (37)/31 (37) (37)/32				Y 			ese liser frant Iser frant frant frant frant		
of Frontes C1 * * * * * * * * * * * * * * * * * *	0 days 07 36 days 07 36 days 07 28 days 07 28 days 07 24 days 07 45 days 07 45 days 07 45 days 07 46 days 07 16 days 07 16 days 07 16 days 07 16 days 07 14 days 07 14 days 07 15 days 17 90 days 18 170 days 19 18 days 17	(39) (37)/30 (37) (37)/31 (37) (37)/31 (37) (37)/31 (37) (37)/32		↓ ↓ ↓ ↓ ↓ ↓ ↓ ↓							
se - India Saray Action Ubanhag we at Portino (2 exe - India Navy) - Construction - Construction	36 days 97 30 days 97 30 days 97 28 days 97 9 days 97 9 days 97 9 days 97 30 days 97 30 days 97 30 days 97 30 days 97 16 days 97 14 days 97 90 days 97 90 days 97 94 days 97 94 days 97	195 07.53 151 196 07.64 154 196 07.64 155 164 196 07.64 155 164 197 07.62 156 164 197 07.62 197.65 164 197 07.62 197.67 164 197 07.62 197.67 164 197 07.62 197.67 164 197 07.62 197.67 164 197 07.63 167.67 164 197 07.64 167.67 164 197 07.64 167.67 164 197 07.64 167.67 164 197 07.64 167.12 167.64									
Honolog Honolog Key Tortion (2 Key Source) Key Source) Key Source) Key Source	28 days 07 164 days 07 0 days 07 45 days 07 30 days 07 30 days 07 16 days 07 16 days 07 14 days 07 14 days 07 90 days 07 39 days 07 30 day	710 37.8.6 153.148 711 07.7.13 57.8.7 512 07.8.23 154 513 07.8.23 154 514 07.8.23 154 517 07.8.23 154 518 07.11 1045-7 517 07.8.1 1945-53 517 07.8.1 15495-53 512 07.8.1 15495-53 512 07.8.1 15495-53 512 07.8.1 15495-53 513 07.1.2 164 514 15.9 164									
which of performs C2 of hermines C2 which is the constraint of the constraint of the constraint of the constraint of	161 days 07 0.days 07 45 days 07 30 days 07 30 days 07 60 days 07 16 days 07 90 days 07 16 days 07 16 days 07 14 days 07 96 days 07 99 days 07 99 days 07 90 days 07 90 days 07 90 days 07	101 101/219 101 107.12 102 107.12 107 105.25 108 106.85 107 105.25 108 106.85 109 101.85 109 101.85 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 07.11 119 04.1 119 04.1							4		
et Forline C2 exe - fordal Stronge exes fordal Stronge exesting Architects exests as A Experiming exests as Technical for finge finge finge for a Stronge Report for any as A Experiment for any as A Experiment	0 days 07 45 days 07 30 days 07 60 days 07 16 days 07 16 days 07 14 days 07 14 days 07 90 days 07 90 days 07 90 days 07 90 days 07	7/3 07 12 12 07.83 158 168 727 07.83 15985.00 50 710 07.83 15985.00 50 717 16985.70 498.156 50 718 07.11 16985.50 405 717 16985.50 405 80 718 17.97 164 8.50 107.12 718 164 14 4 8.50 107.12							1999 - 1999 -	an ann an an an a	
nex - India Funcy cickina Thoulong ey & Royaning ey & Royaning	45 days (07 30 days (07 30 days (07 60 days (07) 16 days (07) 14 days (07) 14 days (07) 90 days (07) 99 days (07) 99 days (07)	9/12 07.8×25 156 717 07.8×25 15948-301.dixs 8/17 07.9×17 16048-72.dips.[56 9/18 07.11 16.16 7/27 07.8×11 1596-53.dix.dixs.s 8/12 07.8×25 16.6 8/26 07.7×12.6 16.4 8/26 07.7×12.5 16.4									
schen schengen schenger Anstanker sone ener Tree Starvy Report Beg Trensen beskaltener Trensen beskaltener Trensen beskaltener schen 20 Starvy schen 20 Starvy Starvy Report Starvy Report St	30 days 07 30 days 07 60 days 07 16 days 07 14 days 07 14 days 07 90 days 07 99 days 07 90 days 07 90 days 07	717 07 8.25 [99F8-3]n days 819 67 917 Jad18-7 days, [56 918 07 11 (6 16) 1 737 u7 8 (1 1 159F8-30 days) 1 819 07 11 (5 16) 1 1 826 u7 9 8 25 163 1 1 826 u7 9 8 164 1 1 826 u7 9 8 164 1 1						6 1988-111-1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997 - 1997	annan an anns an anns an An Stàiteannan an Stàiteannan an Stàiteannan Anns an Stàiteannan Anns an Anns an Anns an Anns an Anns an Anns a An Stàiteanna Anns an An		an ana ana ang ang ang ang ang ang ang a
I Houding conting enhances on & Repetting the second second second second ing mission shuff atom insteam dy before? A second second second second enhances at Jordine C4 of Pertina C4 of Pertina C4	30 days 07 60 days 07 16 days 07 14 days 07 90 days 07 90 days 07 90 days 07 90 days 07 90 days 07	8 19 07 9 17 160198-7 days, 156 9 18 07 11 16 161 7 27 07 8 11 1998-5 in days 8 12 07 8 28 163 8 36 07 9 8 164 8 36 07 13 28 164							ano ano ana serie de serie de Serie de serie		ana ananananan mutanan L
existing articles: «) & Repeting exists of tree Starsey's Report g ting transee Mediathous transee Mediathous transee Mediathous Stream (h) + 640-7 sork at Portlan C4 of Portlan C4 mex - India Starsey	60 days 07 16 days 07 14 days 07 14 days 07 90 days 07 99 days 07 99 days 07 84 days 07	9 18 07 11 16 161 7.27 078 11 15955-30 days 8 12 078 25 163 8 26 07 9 8 164 8 26 07 11 23 164			- -						
scy & Reporting science Trace Stavys Report 6 fing foreament booklations for some thy softwart / science at Portland C4 of Portland C4 max - facial Startacy	16 days 07 14 days 07 14 days 07 14 days 07 90 days 07 99 days 07 84 days 07	x 12 07 x 25 163 x 26 07 9/ x 164 x 26 07 11 23 164			٠ <u>ــــــــــــــــــــــــــــــــــــ</u>						
konk on Tree Survey Report B transet Bodallation transet Bodallation transet Bodallation Sock at Partim C4 of Portion C4 may - India Survey	14 days 07 14 days 07 90 days 07 99 days 07 90 days 07 84 days 07	8.26 07.978-164 8.26 07.11-23 164			C.B.						
ing trimest Installation issum (b) other) sock at Portion C4 of Portion C4 me - Instita Survey	90 days 0 99 days 0 90 days 0 84 days 07	8 26 67 11 23 164	the second	1 2							
trument Installations is ison (b) ethers) sork at Portiun C4 of Portiun C4 mee - Indial Survey	99 davs 0 90 days 0 84 days 67										
hrason (by others) sork at Portion C4 of Portion C4 mee - Initial Survey	90 days 10 84 days 67.		1 .					acculate several partice and and			
vork at Portion C4 of Portion C4 mee - Initial Survey	84 days 67.	9 12 07 12 19 160FS-3 days 9 13 07 12 16 161									
of Portion C4 mce + Initial Survey	84 days 07										
nice · Initial Survey	0 days 07	10/11 00/1/2 10/11 07/10/11									
	28 days 07	le 11 e7.11.7 170	mail as a financia		€_ien LL.h		a mana na sina ana ana ang ang ang ang ang ang ang a				
	42 days 0		-		11 112	1		2			
of Hearding	21 days 07	12/13 08/1/2/172.161						1.2.2	× *		
with Villagers		3 30 07 6 22 143	tienet.	Contraction of the							
A and preparation	62 days 0	6-23 07.8.23. 174				I	1 				
lation	8 days - 0	18:24 07:3:31 175			I GLI						
50							t.				
and which will be							Lip				
ong no chung Read	240 0393 00	10/20 09/1/18				nin the second second second second second		•			
4	97 days 01	10.20 08.1.24 156.45.46.162FN-40 days						·····			
2	103 days 0	10.26 08.2.5 1818S+7 days									
6	55 days	7 12 6 08 1 29 18288+40 days,166									
ince Access & Footpath			100 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	1		1		1			
nd Form access	14 days 00						T				
car Retaining Wall G) Stage 1	45 days 18	11 11 08 12 25 185			1 11		1				
car Che Kung Temples Stage 2	Jui days in	12 26 : 09 1 24 186									
						1 mar					
a a						Land Land					
			and the second second		· · · · · · · · · · · · · · · · · · ·	Gran	and the second sec				
	30 days	8 5 22 08 6 29 191	£	1		11 1					
• 16	105 days .	8 5 24 08 9 5 192				4					
6						11	Cristical and				
2											
	77 days						.	Komono h	1		
lope (Ch 480 00 to 565.00)	28 days	18/11/1 : 08/11-28/184FS-79 days, 193					1 <u>11</u>	20			
werr (near Che Kong Temple)	oli daya b	21129 09127 197				-					
						pana and	C. C	a 1			
							New Protection	The second se			
90 to 290.00							1				
Fung Shui Weir	22 days	19/1/24 09/2/14/201						(B)			
Fishnay	30 days	09:2-15 09:3-16 203						Lines -	and the second second		
flope (Ch 290.00 to 315.00)			and a commenter		alan Ilan		and a second				
								قنيب آ			
			name in the second								
entation of TTA scheme	600 days				- Breeze						
sh existing Ford	21 days								in the second		
alvert RC3	93 days	09 1 15 09 4 17 210		teres constant in the second			T T		a contraction of the second		
einstalment				0.0	1						
Wall H						A THE REAL PROPERTY OF A DESCRIPTION OF					
-3	32 days	07.12.4 08.1.4			1 1	叫打.					
	39 days	ax 1-3m ax-3. x 214	and the second second	a de la competition de	a las de finis	- III Cast	*****	n haine han hanne he	and a fait of the second	teres - as a	
							14	TTTL I			
				C				Co.			
ad radi WSDPS)			1					That			
faintenance Access Ramp	S6 days	09 2 4 09 4/30 217	and a second					Training the set of the			
Wall E	305 days	08/1/12 08/11/11	participante ancorra					TTT	and the second se		
- 6	63 days	08 1 12 08 3 14 214FS-3 days 182FS-37 days				Warner to					
-3				Keel I		1					
			1				No the second se				
rks	556 dayx	07/7/2 09/1/7	L		1		1.1.3				
	mg Ho Chang Bood att G 4 2 4 4 5 4 5 5 6 5 7 7 7 1 1 1 1 5 7 7 7 7 1 1 1 5 7 7 7 7 1 1 1 5 7 7 7 7 7 7 1 1 1 5 7 7 7 7 7 7 7 7 7 7 7 7 7	H 409 Fit Bit Coung Each S2 40 ap. FO All Carl S2 40 ap. FO All Carl S2 40 ap. FO All Carl S3 40 ap. FO 1 S3 40 ap. FO 2 S3 40 ap. FO 4 FO S3 40 ap. FO a Car Strapping	114.00 10.14 10.12 17 126 Chang Bolds 264 dags 10.12 10.75 141 C 254 dags 10.12 10.75 141 C 10.34 0.71028 10.12 17.5 1 10.34 0.71028 10.12 10.25 11.51 14.65 1 10.34 0.7152 0.82.5 11.51 14.65 10.12 <td>H 439 W 10 10 <thw 10="" 10<="" th=""> <thw 10="" 10<="" th=""> <thw 1<="" td=""><td>H 439 W 10 W 10 W 10 W 10 W 10 T 17 Bid 6. W 10 W 10 W 10 W 10 T 10 </td><td>Haday We Hold Hold Program Del Loung Baod 26 days We 1021 175 alt C 47 days 771020 W0 112 185 21 alt C 47 days 771020 W0 112 163 24 175 alt C 100 days 771020 W0 112 163 25 1188 7 days a Sanso 31 days W1 12 663 25 1188 7 days 400 a Formation 11 days W1 12 163 25 1188 7 days 400 a Formation 11 days W1 12 163 25 164 400</td><td>H 440 W 10 H <thw 10="" h<="" th=""> W 10 H <thw 11="" h<="" th=""> <thw 11="" h<="" th=""> <thw 11="" h<="" th=""></thw></thw></thw></thw></td><td>Hoto, Woll, Boal Hoto, Woll, Boal<</td><td>Hote Description Note (Note 1) Note (Note 1) AC AC Apple (Note 1) Note (Note 1) AC Apple (Note 1) Note (Note 1) Note (Note 1) AC Note A Fungal Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) <td< td=""><td>Integra Integra <t< td=""><td>Index Index <th< td=""></th<></td></t<></td></td<></td></thw></thw></thw></td>	H 439 W 10 10 W 10 10 <thw 10="" 10<="" th=""> <thw 10="" 10<="" th=""> <thw 1<="" td=""><td>H 439 W 10 W 10 W 10 W 10 W 10 T 17 Bid 6. W 10 W 10 W 10 W 10 T 10 </td><td>Haday We Hold Hold Program Del Loung Baod 26 days We 1021 175 alt C 47 days 771020 W0 112 185 21 alt C 47 days 771020 W0 112 163 24 175 alt C 100 days 771020 W0 112 163 25 1188 7 days a Sanso 31 days W1 12 663 25 1188 7 days 400 a Formation 11 days W1 12 163 25 1188 7 days 400 a Formation 11 days W1 12 163 25 164 400</td><td>H 440 W 10 H <thw 10="" h<="" th=""> W 10 H <thw 11="" h<="" th=""> <thw 11="" h<="" th=""> <thw 11="" h<="" th=""></thw></thw></thw></thw></td><td>Hoto, Woll, Boal Hoto, Woll, Boal<</td><td>Hote Description Note (Note 1) Note (Note 1) AC AC Apple (Note 1) Note (Note 1) AC Apple (Note 1) Note (Note 1) Note (Note 1) AC Note A Fungal Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) <td< td=""><td>Integra Integra <t< td=""><td>Index Index <th< td=""></th<></td></t<></td></td<></td></thw></thw></thw>	H 439 W 10 W 10 W 10 W 10 W 10 T 17 Bid 6. W 10 W 10 W 10 W 10 T 10	Haday We Hold Hold Program Del Loung Baod 26 days We 1021 175 alt C 47 days 771020 W0 112 185 21 alt C 47 days 771020 W0 112 163 24 175 alt C 100 days 771020 W0 112 163 25 1188 7 days a Sanso 31 days W1 12 663 25 1188 7 days 400 a Formation 11 days W1 12 163 25 1188 7 days 400 a Formation 11 days W1 12 163 25 164 400	H 440 W 10 H W 10 H <thw 10="" h<="" th=""> W 10 H <thw 11="" h<="" th=""> <thw 11="" h<="" th=""> <thw 11="" h<="" th=""></thw></thw></thw></thw>	Hoto, Woll, Boal Hoto, Woll, Boal<	Hote Description Note (Note 1) Note (Note 1) AC AC Apple (Note 1) Note (Note 1) AC Apple (Note 1) Note (Note 1) Note (Note 1) AC Note A Fungal Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) A Apple (Note 1) Note (Note 1) Note (Note 1) <td< td=""><td>Integra Integra <t< td=""><td>Index Index <th< td=""></th<></td></t<></td></td<>	Integra Integra <t< td=""><td>Index Index <th< td=""></th<></td></t<>	Index Index <th< td=""></th<>

