

JOB NO.: TCS00310/06

VERSION NO.: 2

**DRAINAGE SERVICES DEPARTMENT
CONTRACT NO.: DC/2005/02**





**CONSTRUCTION OF SEWERS, RISING MAINS &
SEWAGE PUMPING STATION AT KAM TIN, NAM
SANG WAI AND AU TAU IN YUEN LONG**

**MONTHLY ENVIRONMENTAL MONITORING &
AUDIT (EM&A) REPORT FOR APRIL 2010 (NO.
49) (DESIGNATED ELEMENTS)**

PREPARED FOR

**LEADER CIVIL ENGINEERING CORPORATION
LIMITED**

Quality Index

Date	Reference No.	Prepared By	Certified By	Approved By	Verified By
13 May 2010	TCS00310/06/600/R1078v2	Ben Tam	David Yeung	TW Tam	Dr. Anne F Kerr
					
Environmental Consultant	Environmental Team Leader	General Manager	Independent Environmental Checker		

Version No.	Date	Remarks
1	6 May 2010	First Submission
2	13 May 2010	Amended against IEC's comments

This report has been prepared by Action-United Environmental Services & Consulting with all reasonable skill, care and diligence within the terms of the Agreement with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above. This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies upon the report at their own risk.



Your Ref:
Our Ref: J0511/03.08/9909/L
Date: 14 May 2010

Director of Environmental Protection
27/F Southorn Centre
130 Hennessy Road
Wan Chai, Hong Kong

By Hand

Attention: EIAO Register Office

Dear Sir,

Contract No. DC/2005/02
Construction of Sewers, Rising Mains and Sewage Pumping Station at Kam Tin
Nam Sang Wai and Au Tau in Yuen Long
Submission of Monthly EM&A Report for Designated Project – April 2010
(EP-220/2005 Condition 5.5)

We are pleased to submit 3 hard copies and 1 soft copy of the captioned EM&A report certified by the ETL and verified by the HEC in accordance with EP Condition 5.5 for your retention.

Should you have any queries, please do not hesitate to contact the undersigned on Tel 2443 9835.

Yours faithfully
For and on behalf of
Leader Civil Engineering Corporation Limited

Vincent Chan
Site Agent

VC/mt

Encl.

cc Mott Connell - Dr Anna Kerr / SM Foo Fax: 2827 1823 (1 hard copy + 1 soft copy)
AUES - Mr. David Yeung Fax: 2959 6079 (w/o encl.)
Jacobs China - Mr. Chan Yiu Fai Fax: 2443 9847 (1 hard copy)

Leader Civil Engineering Corporation Ltd.

Units 1001-1015, 10/F Grand Central Plaza, Tower 1, 138 Shatin Rural Committee Road, Sha Tin, N.T., Hong Kong Tel: (852) 2272 3680 Fax: (852) 2375 3655
利達土木工程有限公司 香港新界沙田鄉事會路一三八號新城市中央廣場第一座十樓1001至1015室 電話: (852) 2272 3680 傳真: (852) 2375 3655
A MEMBER OF BUILD KING HOLDINGS 利達控股集團成員

EXECUTIVE SUMMARY

- ES01. Leader Civil Engineering Corporation Limited (the Contractor) has been awarded the DSD Contract DC/2005/02 Construction of Sewers, Rising Mains and Sewage Pumping Station at Kam Tin, Nam Sang Wai and Au Tau in Yuen Long (the Project). The Project requires an Environmental Monitoring and Audit (EM&A) program to be implemented by an Environmental Team (ET) throughout the contract period in compliance with the requirements as stated in the project Environmental Permit (EP-220/2005) and the Project's Updated EM&A (Designated Elements) Manual.
- ES02. This Monthly Environmental Monitoring and Audit (EM&A) Report for **April 2010 (No. 49)** presents the environmental impact monitoring and audit (EM&A) program conducted from **1 to 30 April 2010** for the Designated Elements. The EM&A program in **April 2010** covered air quality, construction noise and waste management only.

BREACH OF ACTION AND LIMIT (AL) LEVELS

- ES03. There were no breaches of Action or Limit level for air monitoring in this reporting month.
- ES04. No construction noise complaint (Action Level) or exceedance was recorded in this reporting month.

COMPLAINT LOG

- ES05. No environmental complaint was received in this month.

NOTIFICATION OF ANY SUMMONS AND SUCCESSFUL PROSECUTION

- ES06. There was no environmental summons or prosecution in this month.

REPORTING CHANGES

- ES07. There are no changes in the reporting format or content in this month.

FUTURE KEY ISSUES

- ES08. Construction activities to be undertaken in **May 2010** include backfilling, concreting and extract sheet pile. Potential environmental impacts arising from the works include construction waste, air quality, noise and water quality (particularly site runoff during rainy seasons). Environmental mitigation measures will be properly implemented and maintained as per the Mitigation Implementation Schedule to ensure site environmental performance is acceptable.

TABLE OF CONTENTS

1.0 BASIC PROJECT INFORMATION.....	1
2.0 ENVIRONMENTAL STATUS	2
3.0 SUMMARY OF EM&A REQUIREMENTS.....	4
4.0 IMPLEMENTATION STATUS	5
5.0 MONITORING RESULTS.....	6
6.0 REPORT ON NON-COMPLIANCE, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS	11
7.0 OTHERS.....	12

LIST OF TABLES

TABLE 2-1 WORK UNDERTAKEN AND ILLUSTRATIONS OF MITIGATION MEASURES
TABLE 2-2 DESCRIPTION OF THE MONITORING STATIONS
TABLE 3-1 SUMMARY OF EM&A REQUIREMENTS
TABLE 3-2 ACTION AND LIMIT LEVELS FOR AIR QUALITY
TABLE 3-3 ACTION AND LIMIT LEVELS FOR CONSTRUCTION NOISE
TABLE 4-1 STATUS OF ENVIRONMENTAL LICENSES AND PERMITS
TABLE 5-1 MONITORING EQUIPMENT USED IN IMPACT EM&A PROGRAM
TABLE 5-2 LOCATION OF AIR QUALITY AND CONSTRUCTION NOISE MONITORING STATIONS/LOCATIONS
TABLE 5-3 SUMMARY OF AIR QUALITY MONITORING RESULTS
TABLE 5-4 SUMMARY OF NOISE MONITORING RESULTS AT NM3
TABLE 5-5 SUMMARY OF NOISE MONITORING RESULTS AT NM4
TABLE 5-6 SUMMARY OF NOISE MONITORING RESULTS AT NM6
TABLE 5-7 SUMMARY OF NOISE MONITORING RESULTS AT NM7
TABLE 5-8 MONITORING SCHEDULE FOR THE NEXT MONTH
TABLE 7-1 SUMMARY OF WASTE QUANTITIES FOR DISPOSAL
TABLE 7-2 SUMMARY OF WASTE QUANTITIES FOR REUSE/RECYCLING

LIST OF ANNEXES

ANNEX A PROJECT SITE LAYOUT
ANNEX B PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE
ANNEX C CONSTRUCTION PROGRAM
ANNEX D PHOTOGRAPHICAL RECORDS – NOISE BARRIER ON-SITES
ANNEX E LOCATIONS OF MONITORING STATIONS
ANNEX F EVENT AND ACTION PLAN
ANNEX G MITIGATION IMPLEMENTATION SCHEDULE
ANNEX H EQUIPMENT CALIBRATION CERTIFICATES
ANNEX I METEOROLOGICAL DATA
ANNEX J GRAPHICAL PLOTS OF AIR QUALITY AND CONSTRUCTION NOISE MONITORING RESULTS
ANNEX K PROFORMA OF SITE INSPECTION AND IEC AUDIT

1.0 BASIC PROJECT INFORMATION

- 1.01 Leader Civil Engineering Corporation Ltd (the Contractor) has been awarded the DSD Contract DC/2005/02 Construction of Sewers, Rising Mains and Sewage Pumping Station at Kam Tin, Nam Sang Wai and Au Tau in Yuen Long (the Project). The Project is part of the Yuen Long and Kam Tin Sewerage and Sewage Disposal (YLKTSSD) Scheme. A site layout map showing the site boundary and the work areas is shown in [Annex A](#).
- 1.02 This Monthly EM&A Report for [April 2010 \(No. 49\)](#) (Designated Elements – Construction Phase) summarizes the impact monitoring results and audit findings from [1 to 30 April 2010](#).

PROJECT ORGANIZATION

- 1.03 The organization chart and lines of communication with respect to the on-site environmental management and monitoring program are shown in [Annex B](#).

CONSTRUCTION PROGRAM OF THIS MONTH

- 1.04 A construction program showing the construction work undertaken in this month is shown in [Annex C](#). Environmental mitigation measures implemented are given in [Table 2-1](#).

MANAGEMENT STRUCTURE

- 1.05 The management structure of the Project is provided in [Annex B](#).

CONSTRUCTION ACTIVITIES UNDERTAKEN IN THIS MONTH

- 1.06 The major construction activities undertaken during this month under the Environmental Permit (EP-220/2005) were as follows:-

Location	Construction Activities					
	Sheet piling	Excavation	Pipe laying	Backfilling	Concreting	Extract Sheet Pile
Kam Tin Pumping Station(P1)		X		X	X	
Sha Po Pumping Station(P2)						
Nam Sang Wai P/S(P3)					X	
Nam Sang Wai Road(S4)					X	X
Pok Wai South Road(S5 & S6)	X	X	X	X	X	X

2.0 ENVIRONMENTAL STATUS

WORKS UNDERTAKEN IN THIS MONTH

2.01 A summary of the works undertaken in this month with illustrations and environmental mitigation measures implemented is shown in [Table 2-1](#).

Table 2-1 Work Undertaken and Illustrations of Mitigation Measures

Locations	Description of Construction Activities	Environmental Mitigation Measures	EM&A Ref.
P1 (Kam Tin Pumping Station)	<ul style="list-style-type: none"> ● Excavation ● Backfilling ● Concreting 	<ul style="list-style-type: none"> • Erect 2.4m high noise barrier hoarding around the works area at P1, P2 and P3 • Remove dust and spray water at the construction access • Cover the stockpiles of dusty material properly • Spray water to all dusty materials immediately before loading and unloading 	A1 & F6 A2 A3 A4
P2 (Sha Po Pumping Station) and	<ul style="list-style-type: none"> ● Nil 	<ul style="list-style-type: none"> • Erect 2.4m high noise barrier hoarding around the works area at P1, P2 and P3 • Remove dust and spray water at the construction access • Cover the stockpiles of dusty material properly • Spray water to all dusty materials immediately before loading and unloading 	A1 & F6 A2 A3 A4
P3 (Nam Sang Wai Pumping Station)	<ul style="list-style-type: none"> ● Concreting 	<ul style="list-style-type: none"> • Erect 2.4m high noise barrier hoarding around the works area at P1, P2 and P3 • Wash the wheels of vehicles before leaving the site • Install and use power-operated cover at the dump trucks • Spray water at the pavement breaking locations • Spray the working area of excavation frequently • Maximize the use of quiet PME on site • Apply and obtain appropriate waste disposal licenses 	A1 & F6 A5 A6 A7 A8 B1, B2 & F5 D1
S4 (Nam Sang Wai Road) and	<ul style="list-style-type: none"> ● Concreting ● Extract sheet pile 	<ul style="list-style-type: none"> • Remove dust and spray water at the construction access • Cover the stockpiles of dusty material properly • Spray water to all dusty materials immediately before loading and unloading • Wash the wheels of vehicles before leaving the site 	A2 A3 A4 A5
S5 & S6 (Pok Wai South Road)	<ul style="list-style-type: none"> ● Sheet piling ● Excavation ● Pipe laying ● Backfilling ● Concreting ● Extract sheet pile 	<ul style="list-style-type: none"> • Handle, store and dispose of chemical wastes as per relevant regulations • Implement trip-ticket system for waste disposal • Restrict open fires and provide fire fighting equipment in the works area • Perform weekly inspection with ET and monthly audit with IEC • Conduct noise and dust monitoring as per EM&A Manual during construction • Provide sedimentation tanks for treating site discharge. • Recycle wheel washing water and provide sedimentation tanks for treating site discharge. 	D2, D3 & D4 D5 F9 H1 I1 & I2 - -

2.02 Photographic records showing the implemented 2.4m high noise barrier at the pumping station (S3) are shown in [Annex D](#).

PROJECT DRAWINGS

2.03 Drawings showing the work areas under EP-220/2005 and the locations of the designated monitoring stations are presented in [Annex E](#).

2.04 There are four designated air quality monitoring stations (AM1, AM5, AM6 & AM7) and four noise monitoring stations (NM3, NM4, NM6 & NM7) under the project EP. Locations of the monitoring stations and description are summarized in **Table 2-2**.

Table 2-2 Description of the Monitoring Stations

Station ID	Nature of Premise	Site Work Description	Station Coordinates	
			Northern	Eastern
AM1	Site Boundary in NSW	excavation; sheet piling; backfilling; pipe laying; concreting; and extract sheet pile	835829	822910
AM5	Site Boundary in FKH		835121	823515
AM6	Site Boundary in KT		833308	823987
AM7	Site Boundary in NSW		836171	822586
NM3	Village House in NSW		835808	822817
NM4	Village House in NSW		835282	822811
NM6	Village House in KT		833288	823999
NM7	Village House in FKH		835121	823495

3.0 SUMMARY OF EM&A REQUIREMENTS

MONITORING PARAMETERS

- 3.01 Environmental monitoring and audit requirements are set out in the Updated EM&A Manual. Air quality and construction noise have been identified as the key monitoring parameters during the construction phase of the project.
- 3.02 A summary of the impact EM&A requirements for air quality and construction noise is shown in [Table 3-1](#).

Table 3-1 Summary of EM&A Requirements

Environmental Aspect	Monitoring Parameters
Air Quality	24-hour TSP
Construction Noise	Leq 30min day time 07:00 to 19:00 (Supplementary L10 and L90 for reference.)

ENVIRONMENTAL QUALITY PERFORMANCE LIMITS

- 3.03 A summary of the Action/Limit (A/L) Levels for air quality and construction noise is shown in [Tables 3-2](#) and [3-3](#).

Table 3-2 Action and Limit Levels for Air Quality

Monitoring Locations	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
AM1	> 391	> 184	> 500	> 260
AM5	> 353	> 237	> 500	> 260
AM6	> 329	> 183	> 500	> 260
AM7	> 383	> 204	> 500	> 260

Table 3-3 Action and Limit Levels for Construction Noise

Monitoring Period	Action Level	Limit Level
0700-1900 hours on normal weekdays	When one or more documented complaints are received	> 75 dB(A)

EVENT AND ACTION PLANS

- 3.04 An Event Action Plan for air quality and construction noise has been implemented for this project. Details of the Event Action Plan are presented in [Annex F](#).

ENVIRONMENTAL MITIGATION MEASURES

- 3.05 The project EIA report has recommended environmental mitigation measures to minimize potential environmental impacts arising from the construction of the project. A full list of the mitigation measures is detailed in [Annex G](#).

ENVIRONMENTAL REQUIREMENTS IN CONTRACT DOCUMENTS

- 3.06 The environmental requirements in the contract documents generally refer to the compliance of the requirements as stipulated in the project EP (EP-220/2005) and the updated EM&A Manual.

4.0 IMPLEMENTATION STATUS

- 4.01 The implementation status of environmental protection and pollution control/mitigation measures as recommended in the project EIA report are summarized in [Table 2-1](#) and the implementation schedule as shown in [Annex G](#).
- 4.02 The status of permits, licenses, and/or notifications related to environmental protection under this Project during the month is presented in [Table 4-1](#).

Table 4-1 Status of Environmental Licenses and Permits

Items	Item Description	License/Permit Status
1	Environmental Permit No.: EP-220/2005	Issued in June 2005
2	Air Pollution Control (Construction Dust)	Notified EPD on 24 Dec 2005
3	Chemical Waste Producer Registration (No. 5213-528-L2544-08)	Registration on 27 Jan 2006
4	Water Pollution Control (Discharge License No. 1U434/1)	Issued on 8 May 2006
5	Account for Disposal of Construction Waste No. 5004959	Registration on 27 Dec 2005

5.0 MONITORING RESULTS

MONITORING METHODOLOGY OF AIR QUALITY MONITORING

- 5.01 The 24-hour TSP monitoring was carried out by a High Volume Air Sampler (HVAS) in compliance with the updated EM&A Manual. The HVAS employed complies with the PS specifications including.
- Power supply of 220v/50 Hz for 24-hour continuous operation;
 - 0.6-1.7m³/min (20-60 SCFM) adjustable flow rate;
 - A 7-day mechanical timer for 24-hour operation;
 - An elapsed time indicator with ± 2 minutes accuracy for 24-hour operation;
 - Minimum exposed area of 63in²;
 - Flow control accuracy of $\pm 2.5\%$ deviation over 24-hour operation;
 - An anodized aluminum shelter to protect the filter and sampler;
 - A motor speed-voltage control to control mass flow rate with accuracy of $\pm 2.5\%$ deviation over 24-hour sampling period;
 - Provision of a flow recorder for continuous monitoring;
 - Provision of a peaked roof inlet;
 - Incorporation with a manometer; and
 - An 8"x10" stainless steel filter holder to hold, seal and easy to change the filter paper.
- 5.02 The filter papers used in 24-hour TSP monitoring were of size 8"x10" and provided by a local HOKLAS-accredited laboratory, ALS Techichem Pty (HK) Limited (HOKLAS No. 66). The filters papers after measurements were returned to the laboratory for the required treatment and analysis. The validation of all monitoring practices and data were following the in-house QA/QC procedures. Blank filters samples were collected and delivered to the HOKLAS-accredited laboratory for QA/QC check.
- 5.03 The meteorological information in this month was obtained from Lau Fau Shan Station of the Hong Kong Observatory (HKO).

METHODOLOGY FOR CONSTRUCTION NOISE MONITORING

- 5.04 Noise measurements were taken in terms of the A-weighted equivalent sound pressure level (Leq) measured in decibels (dB). Supplementary statistical results (L₁₀ and L₉₀) were also obtained for reference.
- 5.05 Hand-held sound level meters and associated acoustical calibrators in compliance with the International Electrotechnical Commission (IEC) Publication 651:1979 (Type 1) and 804:1985 (Type 1) specifications were used for taking the baseline noise measurements.
- 5.06 Windshield was fitted in all measurements. All noise measurements were made with the meter set to FAST response and on the A-weighted equivalent continuous sound pressure level (Leq).
- 5.07 No noise measurement was made in the presence of fog, rain, wind with a steady speed exceeding 5m/s or wind with gusts exceeding 10m/s.

LABORATORY AND MONITORING EQUIPMENT USED

- 5.08 A local HOKLAS-accredited laboratory, ALS Technichem (HK) Pty Ltd (HOKLAS No. 66), is responsible for the analytical testing of the 24-hour TSP filter papers.
- 5.09 Monitoring equipment used in the impact EM&A program is presented in [Table 5-1](#).

Table 5-1 Monitoring Equipment Used in Impact EM&A Program

Env. Aspect	Parameters	Monitoring Equipment
Air Quality	24-hour TSP	Greasby Anderson GMWS2310 High Volume Air Sampler
Noise	Leq(30mins)	B&K Sound Level Meter (Type 2238) and Acoustics Calibrator (Type 4231)

EQUIPMENT CALIBRATION

- 5.10 Initial calibration of the HVAS was performed upon installation and thereafter at a six month intervals in accordance with the manufacturer's instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5025A). The calibration data are properly documented and the records are maintained by ET for future reference. HVAS of AM5 and AM6 was required calibration in this month, HVAS of AM5 and AM6 monitoring equipment required to calibrate in next month. Updated calibration certificate and schedule is shown in **Annex H**.
- 5.11 The sound level meters were calibrated using an acoustical calibrator prior to and after measurements. The meters are regularly calibrated in accordance with the manufacturer's instructions. Prior to and following each noise measurement, the accuracy of the sound level meter was checked using an acoustical calibrator generating a known sound pressure level at a known frequency. Measurements were considered valid only if the calibration levels before and after the noise measurement agree to within 1.0 dB.
- 5.12 Calibration certificates of the sound level meters will provide depend on the annual calibration had undertaken.

PARAMETERS MONITORED

- 5.13 The environmental parameters monitoring in this month were compliance with the monitoring requirements as in **Table 3-1**.

MONITORING LOCATIONS

- 5.14 There are four designated air quality and four noise monitoring stations under the project EP. For this month, monitoring was carried out at four designated air (AM1, AM5, AM6 & AM7) and four noise (NM3, NM4, NM6 & NM7) monitoring stations. The locations of the designated monitoring stations are shown in **Table 5-2** and geographically in **Annex E**.

Table 5-2 Location of Air Quality and Construction Noise Monitoring Stations/Locations

Air Quality (4 Stations)	
AM1	Worksite boundary facing scattered house in Nam Sang Wai
AM5	Worksite boundary facing Fung Kat Heung
AM6	Worksite boundary facing scattered near Route 3
AM7	Worksite boundary facing scattered house in Nam Sang Wai
Construction Noise (4 Locations)	
NM3	Village House in Nam Sang Wai
NM4	Village House in Nam Sang Wai
NM6	Scattered House near Route 3
NM7	Fung Kat Heung

MONITORING FREQUENCY AND PERIOD

- 5.15 The impact 24-hour TSP monitoring was conducted at the designated stations once every 6 days in compliance with the updated EM&A Manual.
- 5.16 In this reporting period, a total of **4** monitoring days were scheduled at designated station AM1, AM5, AM6 and AM7. However, there are **8** events of unsuccessful 24-hour monitoring

due to the power failure of HVS occurred at AM1, AM5, AM6 and AM7.

MONITORING RESULTS AND SCHEDULE

5.17 Monitoring results in this month for air quality is summarized at **Table 5-3**.

Table 5-3 Summary of Air Quality Monitoring Results

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)			
	AM1	AM5	AM6	AM7
9-Apr-10	Power failure#	32	35	Power failure#
15-Apr-10	Power failure#	42	37	Power failure#
21-Apr-10	Power failure#	Power failure#	Power failure#	Power failure#
27-Apr-10	66	125	63	188
Average (Range)	NA	66 (32-125)	45 (35 – 63)	NA
Action / Limit	> 184 / >260	> 237 / >260	> 183 / >260	> 204 / >260

Note: All 24-hour TSP monitoring present was start at 00:00 on each monitoring date.

Monitoring was affected due to power failure.

5.18 In this reporting period, there were no breaches of Action/ Limit level in 24-hour TSP air monitoring. However, a total of **8** events of power failure incident were happened at Station AM1, AM5, AM6 and AM7 as presented in Table 5-3. The ET has liaised with the Contractor for the power supply provision issue and the power at all the station were resumed on 26 April 2010.

5.19 Results of construction Noise monitoring in this month were summarized at **Tables 5-4 to 5-7**.

Table 5-4 Summary of Noise Monitoring Results at NM3

Date	Start Time	1st Leq5	2nd Leq5	3rd Leq5	4th Leq5	5th Leq5	6th Leq5	Leq30	Corrected* Leq30
1-Apr-10	11:30	58.4	59.3	58.8	57.6	57.9	59.1	58.6	61.6
10-Apr-10	11:30	58.2	58.8	57.6	58.3	59.3	59.9	58.7	61.7
16-Apr-10	14:27	51.2	52.6	52.4	51.7	51.4	52.0	51.9	54.9
22-Apr-10	11:05	54.7	54.4	55.6	55.2	56.3	56.6	55.5	58.5
28-Apr-10	11:00	57.4	57.9	57.7	59.7	58.2	57.0	58.1	61.1
Limit Level									75

Note: * A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines.

Table 5-5 Summary of Noise Monitoring Results at NM4

Date	Start Time	1st Leq5	2nd Leq5	3rd Leq5	4th Leq5	5th Leq5	6th Leq5	Leq30	Corrected* Leq30
1-Apr-10	9:55	60.6	60.7	61.4	61.1	63.7	62.0	61.7	64.7
10-Apr-10	10:00	54.9	56.1	56.6	55.8	57.4	56.9	56.4	59.4
16-Apr-10	9:42	50.2	52.3	51.0	49.6	50.4	50.3	50.7	53.7
22-Apr-10	9:30	62.4	62.2	63.1	62.7	65.7	62.5	63.3	66.3
28-Apr-10	9:15	58.2	59.4	59.1	58.2	60.3	59.4	59.2	62.2
Limit Level									75

Note: * A façade correction of +3 dB(A) has been added according to acoustical principles and EPD guidelines.

Table 5-6 Summary of Noise Monitoring Results at NM6

Date	Start Time	1st Leq5	2nd Leq5	3rd Leq5	4th Leq5	5th Leq5	6th Leq5	Leq30
1-Apr-10	13:07	64.8	65.0	64.6	64.5	65.2	64.7	64.8
10-Apr-10	16:39	68.4	68.1	68.7	68.2	68.1	68.0	68.3
16-Apr-10	13:09	67.1	67.6	67.2	66.9	66.9	67.3	67.2
22-Apr-10	13:06	65.4	65.7	65.3	64.9	65.2	65.6	65.4
28-Apr-10	13:09	64.6	64.9	65.0	64.7	64.3	64.9	64.7
Limit Level								75

Note: Noise monitoring was undertaken at the façade, correction was not necessary.

Table 5-7 Summary of Noise Monitoring Results at NM7

Date	Start Time	1st Leq5	2nd Leq5	3rd Leq5	4th Leq5	5th Leq5	6th Leq5	Leq30
1-Apr-10	9:00	58.4	60.7	59.3	59.9	57.9	58.6	59.2
10-Apr-10	9:15	56.9	57.4	56.3	58.4	58.8	56.9	57.5
16-Apr-10	13:24	51.6	50.3	50.5	53.1	5.7	50.8	50.6
22-Apr-10	8:45	60.7	59.4	59.5	58.7	57.4	58.4	59.1
28-Apr-10	9:00	54.9	56.7	57.2	57.7	56.4	57.1	56.8
Limit Level								75

Note: Noise monitoring was undertaken at the façade, correction was not necessary.

5.20 No construction noise complaint (Action Level) was received; and also construction noise monitoring above the Limit Level was recorded in this month.

5.21 The tentative monitoring schedule for the coming month (**May 2010**) is shown in **Table 5-8**.

Table 5-8 Tentative Schedule of Monitoring for Next Month

Date		Air Quality	Noise Leq 30min
Sat	1-May-10		
Sun	2-May-10		
Mon	3-May-10		
Tue	4-May-10		
Wed	5-May-10		
Thu	6-May-10		
Fri	7-May-10		
Sat	8-May-10		
Sun	9-May-10		
Mon	10-May-10		
Tue	11-May-10		
Wed	12-May-10		
Thu	13-May-10		
Fri	14-May-10		
Sat	15-May-10		
Sun	16-May-10		
Mon	17-May-10		
Tue	18-May-10		
Wed	19-May-10		
Thu	20-May-10		
Fri	21-May-10		
Sat	22-May-10		
Sun	23-May-10		
Mon	24-May-10		
Tue	25-May-10		
Wed	26-May-10		

Thu	27-May-10		
Fri	28-May-10		
Sat	29-May-10		
Sun	30-May-10		
Mon	31-May-10		

	Monitoring Day
	Sunday or Public

WEATHER CONDITIONS DURING THE MONITORING MONTH

5.22 The meteorological data during the monitoring date are summarized in [Annex I](#).

GRAPHICAL PLOTS OF TRENDS OF MONITORED PARAMETERS

5.23 The graphical plots of air quality and construction noise monitoring data are presented in [Annex J](#).

WEATHER CONDITIONS THAT AFFECT THE MONITORING RESULTS

5.24 The weather conditions during monitoring were considered acceptable for monitoring activities and did not have significant impact on the monitoring results obtained.

OTHER FACTORS INFLUENCING THE MONITORING RESULTS

5.25 There were no other noticeable external factors generally affecting the monitoring results in this month.

QA/QC RESULTS AND DETECTION LIMITS

5.26 Not applicable.

6.0 REPORT ON NON-COMPLIANCE, COMPLAINTS, NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTIONS

RECORD OF NON-COMPLIANCE OF ACTION AND LIMIT LEVELS

- 6.01 There were no breaches of Action or Limit level for air monitoring in this reporting month.
- 6.02 No construction noise complaint (Action Level) or monitoring noise level exceeding the Limit Level was recorded in this reporting month.

RECORD OF ENVIRONMENTAL COMPLAINTS RECEIVED

- 6.03 There were no environmental complaints received in this month.

RECORD OF NOTIFICATIONS OF SUMMONS AND SUCCESSFUL PROSECUTION

- 6.04 There were no notification of summons or prosecutions received in this month.

REVIEW OF REASONS FOR AND IMPLICATIONS OF NC, COMPLAINTS AND NOS

- 6.05 No complaints or notification of summons was received in this month.

DESCRIPTION OF FOLLOW-UP ACTIONS TAKEN

- 6.06 As mention in Section 6.05, no non-compliance, complaints or notification of summons was received in this month. Therefore, no follow-up action was needed. The Contractor was reminded to implement the environmental mitigation measures as present in **Table 2-1** as necessary.

7.0 OTHERS

FUTURE KEY ISSUES

- 7.01 Construction activities to be undertaken in **May 2010** include backfilling, concreting and extract sheet pile. Potential environmental impacts arising from the works include construction waste, air quality, noise and water quality (particularly site runoff during rainy seasons). Environmental mitigation measures will be properly implemented and maintained as per the Mitigation Implementation Schedule to ensure site environmental performance is acceptable.

SOLID AND LIQUID WASTE MANAGEMENT STATUS

- 7.02 The quantities of waste for disposal or reuse in this month are summarized in **Tables 7-1** and **7-2**.

Table 7-1 Summary of Waste Quantities for Disposal

Type of Waste	Quantity	Disposal Location
C&D Materials (Inert) (tons) – Disposed	242	Tuen Mun 38 Fill Bank
C&D Materials (Inert) (tons) – Reused	0	DSD Contract DC/2005/02
C&D Materials (Non-Inert) (tons)	0	NA
Chemical Waste (Litres)	0	NA
General Refuse (tons)	72	Refuse Collector

Table 7-2 Summary of Waste Quantities for Reuse/Recycling

Type of Waste	Quantity	Disposal Location
Metals for Recycling (kg)	36000	Recycle Company
Paper for Recycling (kg)	0	NA
Plastics for Recycling (kg)	0	NA

- 7.03 There was no site effluent discharged but an estimated volume of less than 50m³ of surface runoff was discharged in the month. The sampling of effluent had been carried out by the Contractor in compliance with the Discharge License (No.1U434/1) requirement in this month.

SUBMISSION OF PROFORMA

- 7.04 Representatives of the Engineer, the Contractor and ET carried out regular weekly site inspection on **9, 14, 20 and 27 April 2010** to evaluate the site environmental performance. No non-compliance was found in this month. **Two** observations were recorded from the ET weekly site inspections. The monthly site audit by the IEC in this reporting month was undertaken on **27 April 2010**. No non-compliance and observation was issued by IEC.
- 7.05 Records of the weekly site inspection and joint IEC site audit are presented in **Annex K**.

ANNEX A


PROJECT SITE LAYOUT

ANNEX B

PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE

**DSD Contract No. DC/2005/02
Construction of Sewers, Rising Mains and Sewage Pumping Station at Kam Tin
Nam Sang Wai and Au Tau in Yuen Long
Contractor's Site Organization Chart**

Rev. 21
Date : Feb 2009

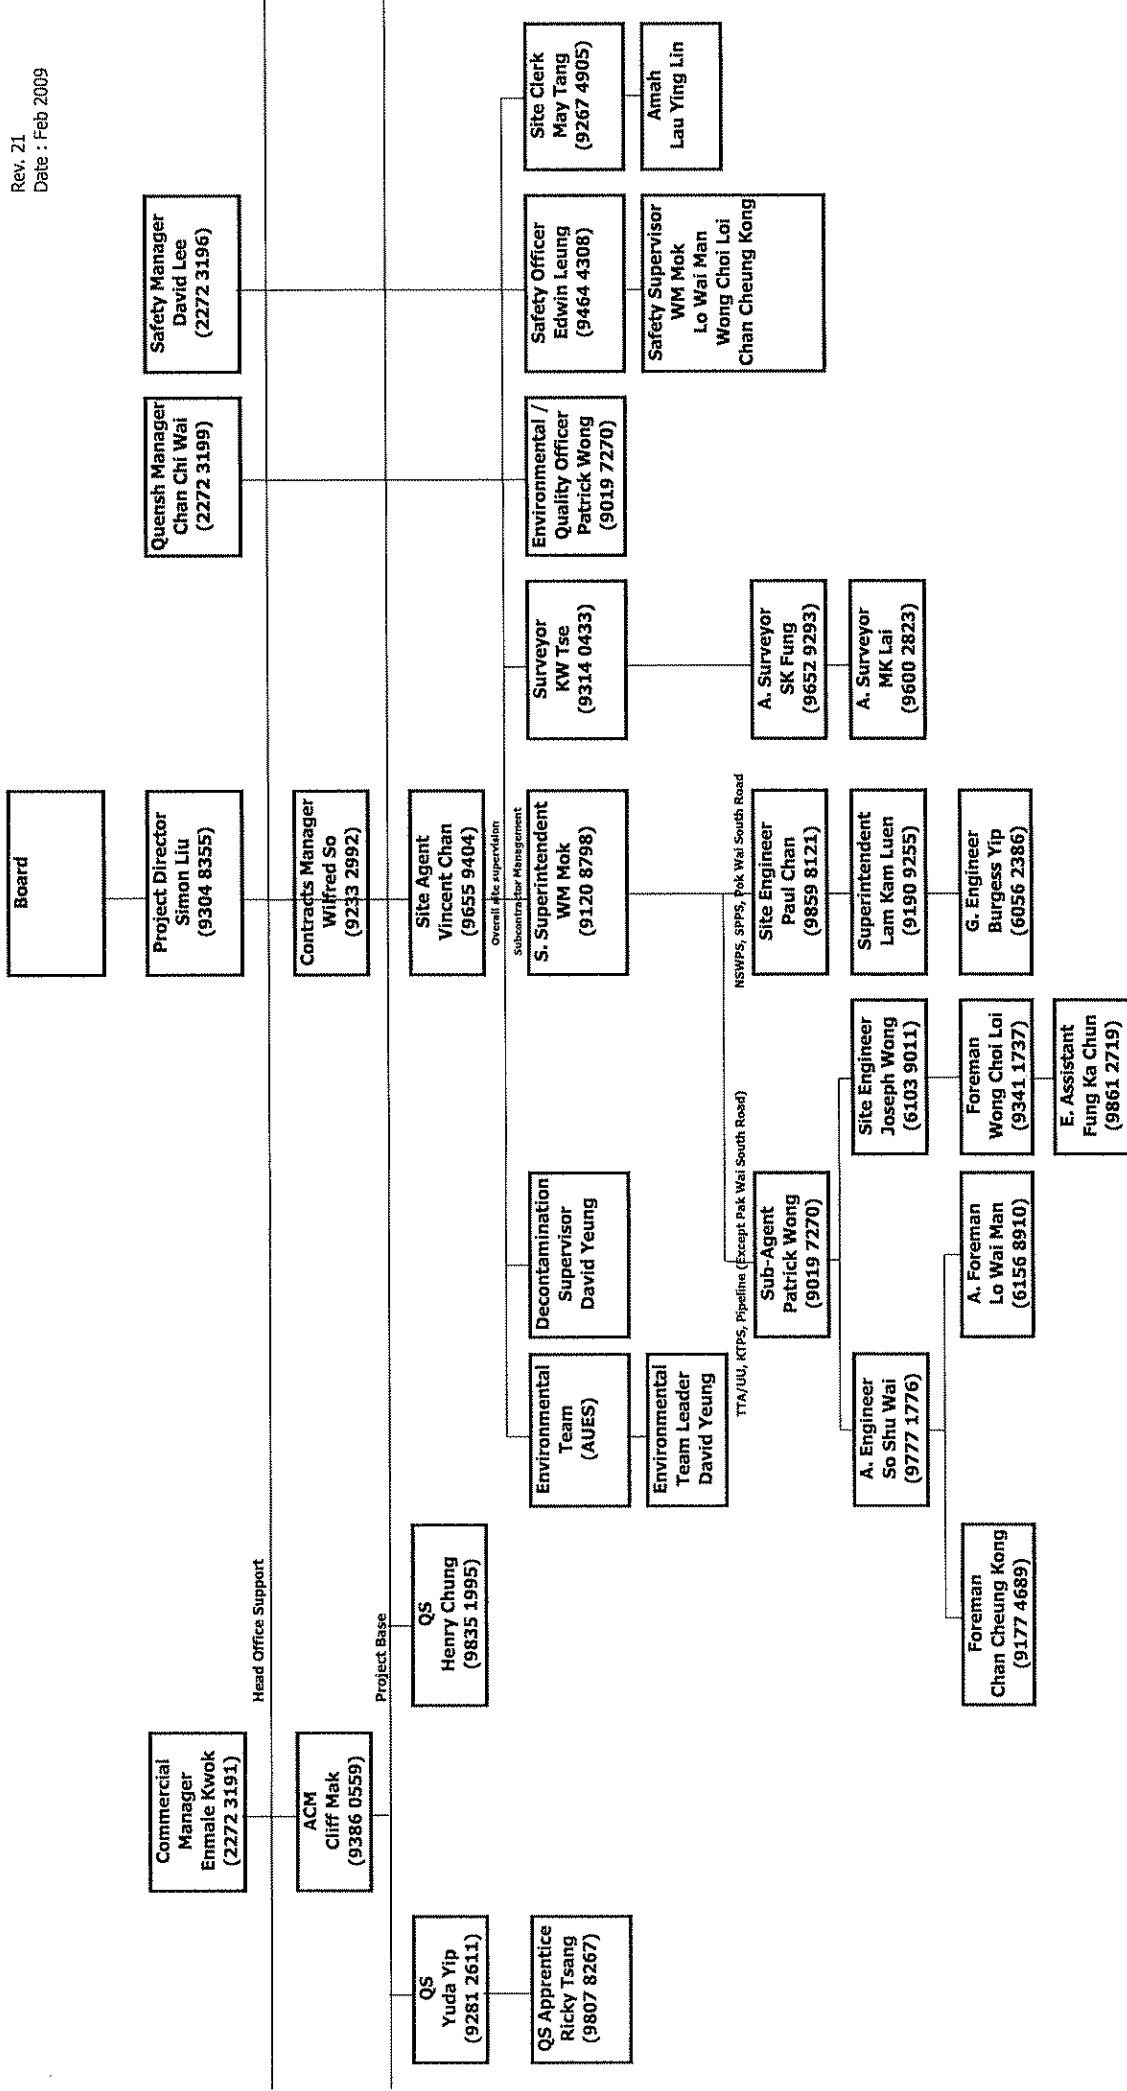

ANNEX C

CONSTRUCTION PROGRAM

Act ID	Description	Orig Dur	Total Float	Percent Complete	Early Start	Early Finish	2006 2007 2008 2009 2010																							
							2006		2007		2008		2009		2010															
Section Completion / Key Date																														
CD9000	Handover of TOA	0	0	0		30MAR10	◆ Handover of TOA																							
Section 1 - Kam Tin Sewage Pumping Station																														
Portion A																														
Fencing																														
S1AD1000	Install Pedestrian Gate	2	0	0	28APR10	29APR10	■ Install Pedestr																							
S1AD1100	Install Vehicle Gates	6	0	0	21APR10	27APR10	■ Install Vehicle																							
S1AD1200	Install Chain Link Fence	4	0	0	16APR10	20APR10	■ Install Chain Lin																							
S1AD1300	Install GMS Panel Fence	8	0	60	24SEP09 A	15APR10	■ Install GMS Pa																							
Drainage and Ducts																														
Trench Method																														
S1AEA1200	DN1050 Pipe & Manhole (P/S - Outfall)	20	0	10	20MAR10 A	21APR10	■ DN1050 Pipe &																							
S1AEA1400	Construct U-Channel & Catchpits	20	0	0	22APR10	15MAY10	■ Construct U-																							
S1AEA1500	Lay Ducts & Construct Drawpits	14	0	0	22APR10	08MAY10	■ Lay Ducts &																							
S1AEA1900	CCTV Inspection of Pipeline	1	0	0	22APR10	22APR10	■ CCTV Inspecti																							
Pipework - Rising Main																														
Trench Method																														
S1AFA1000	Twin Rising Main DN700	20	0	50	15APR10 A	12APR10	■ Twin Rising Mai																							
Earthworks																														
S1AG2700	Trim & Compact Formation of Paved Areas	6	0	0	05MAY10	11MAY10	■ Trim & Comp																							
Roads and Pavings																														
S1AH1000	Lay 250mm Granular Fill Material Base	4	0	0	08MAY10	12MAY10	■ Lay 250mm C																							
S1AH1100	Construct Concrete Paved Areas	18	0	0	13MAY10	02JUN10	■ Construct C																							
S1AH1200	Lay Kerb	4	0	0	11MAY10	14MAY10	■ Lay Kerb																							
In-Situ Concrete																														
S1AL2110	Construct Boundary Wall (stage 2)	10	0	0	31MAR10	12APR10	■ Construct Boun																							
Landscape Softworks and Establishment Works																														
S1AR1000	Preparation Works	6	0	0	15MAY10	21MAY10	■ Preparation																							
S1AR1100	Planting Works	12	0	0	22MAY10	04JUN10	■ Planting W																							

Start date 19DEC05
 Finish date 16SEP10
 Data date 31MAR10
 Page number 1A
 Project name RP15
 Primavera Systems, Inc.

Leader Civil Engineering Corp. Ltd.
DSD Contract No. DC/2005/02
Revised Programme RP15 - 3-Month Rolling Programme for 01 Apr. 2010 to 28 Jun. 2010

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

Act ID	Description	Orig Dur	Total Float	Percent Complete	Early Start	Early Finish	2006 2007 2008 2009 2010																																																																							
							2006				2007				2008				2009				2010																																																							
							E	F	M	A	M	J	J	A	S	O	N	D	E	F	M	A	M	J	J	A	S	O	N	D	E	F	M	A	M	J	J	A	S	O	N	D	E	F	M	A	M	J	J	A	S	O	N	D	E	F	M	A	M	J	J	A	S	O	N	D	E	F	M	A	M	J	J	A	S	O	N	D
Testing																																																																														
S1AS1000	Pressure Testing to Twin Rising Main DN700	12	0	0	01APR10	15APR10	■ Pressure Testin																																																																							
Additional Works / Disruption																																																																														
Combine A4/AIC10 (Claim No. 183)																																																																														
S1AV1250	Construction of AIC13	30	0	10	01MAR10 A	03MAY10	■ Construction c																																																																							
Section 2 - Sha Po Sewage Pumping Station																																																																														
Portion B																																																																														
Fencing																																																																														
S2BD1000	Install Pedestrian Gates	4	0	0	03APR10	08APR10	■ Install Pedestria																																																																							
S2BD1100	Install Vehicular Gates	6	0	90	26FEB10 A	02APR10	■ Install Vehicular C																																																																							
S2BD1200	Install Chain Link Fence	2	0	0	31MAR10	01APR10	■ Install Chain Link																																																																							
Drainage and Ducts																																																																														
Trench Method																																																																														
S2BEA1300	Lay Ducts & Construct Drawpit	6	0	80	05FEB10 A	31MAR10	■ Lay Ducts & Con																																																																							
Landscape Softworks and Establishment Works																																																																														
S2BR1000	Preparation Works	6	0	0	01APR10	08APR10	■ Preparation Wor																																																																							
S2BR1100	Planting Works	12	0	0	09APR10	22APR10	■ Planting Works																																																																							
Section 3 - Nam Sang Wai Sewage Pumping Station																																																																														
Portion C																																																																														
Fencing																																																																														
S3CD1000	Install Chain Link Fence	4	0	0	02APR10	07APR10	■ Install Chain Link																																																																							
Drainage and Ducts																																																																														
Trench Method																																																																														
S3CEA1500	Construct U-channel, Dish Channel & Catchpit	27	0	90	26NOV09 A	01APR10	■ Construct U-char																																																																							
S3CEA1600	Lay Ducts & Construct Drawpit	6	0	90	26NOV09 A	01APR10	■ Lay Ducts & Con																																																																							
Landscape Softworks and Establishment Works																																																																														
S3CR1000	Preparation Works	6	0	0	02APR10	09APR10	■ Preparation Wor																																																																							
S3CR1100	Planting Works	12	0	0	10APR10	23APR10	■ Planting Works																																																																							
Miscellaneous																																																																														
S3CT1300	Plumbing Work	24	0	95	18JUN09 A	31MAR10	■ Plumbing Work																																																																							
S3CT1500	Install FRP Water Storage Tanks	12	0	0	31MAR10	14APR10	■ Install FRP Wa																																																																							

Start date 19DEC05
 Finish date 16SEP10
 Data date 31MAR10
 Page number 2A
 Project name RP15
 Primavera Systems, Inc.

Leader Civil Engineering Corp. Ltd.
DSD Contract No. DC/2005/02
Revised Programme RP15 - 3-Month Rolling Programme for 01 Apr. 2010 to 28 Jun. 2010

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

Act ID	Description	Orig Dur	Total Float	Percent Complete	Early Start	Early Finish	2006												2007												2008												2009												2010											
							E				F				M				A				M				J				J				A				S				O				N				D															
Section 4 - Sewers & RM in Portion D, F, G, H, I																																																																		
Portion D																																																																		
Additional Works / Disruption																																																																		
AIC2																																																																		
S4DV1630	Engineer Confirmation of Pipe Connection	7	0	0	31MAR10	08APR10																									■	Engineer Confir																																		
S4DV1640	Pipe Connection in AIC2	12	0	0	09APR10	22APR10																									■	Pipe Connectio																																		
Portion F																																																																		
Pipework - Rising Main																																																																		
Trench Method																																																																		
S4FFA2600	CCTV Inspection of Pipeline	8	0	0	31MAR10	09APR10																									■	CCTV Inspectio																																		
Portion G																																																																		
Additional Works / Disruption																																																																		
AIC6																																																																		
S4GV1040	Pipe Connection inside Chamber	20	0	0	31MAR10	23APR10																									■	Pipe Connectio																																		
Portion H																																																																		
Pipework - Rising Main																																																																		
Trench Method																																																																		
S4HFA2410	Twin Rising Main DN700 (ChC1550 - ChC1600)	45	0	70	25FEB10 A	04MAY10																									■	Twin Rising M																																		
S4HFA3600	CCTV Inspection of Pipeline	4	0	0	05MAY10	08MAY10																									■	CCTV Inspect																																		
Trenchless Method																																																																		
S4HFB1300	CCTV Inspection of Pipeline	2	0	0	31MAR10	01APR10																									■	CCTV Inspectio																																		
Geotechnical works																																																																		
S4HP1000	Monitoring of Instruments	947	0	86	26MAY06 A	03SEP10																									■	Mo																																		
Additional Works / Disruption																																																																		
S4HV5050	Confirmation of Delay Pipe connection	14	0	0	31MAR10	16APR10																									■	Confirmation of																																		
S4HV5060	Delay Pipe Connection	10	0	0	17APR10	28APR10																									■	Delay Pipe Cor																																		
Portion I																																																																		
Drainage and Ducts																																																																		
Trench Method																																																																		
S4IEA2500	CCTV Inspection of Pipeline	8	0	0	31MAR10	09APR10																									■	CCTV Inspectio																																		
Geotechnical works																																																																		
S4IP1000	Monitoring of Instruments	827	0	85	28JUN06 A	26AUG10																									■	Mo																																		
Miscellaneous																																																																		
Testing																																																																		

Start date	19DEC05
Finish date	16SEP10
Data date	31MAR10
Page number	3A
Project name	RP15
© Primavera Systems, Inc.	

Leader Civil Engineering Corp. Ltd.
DSD Contract No. DC/2005/02
Revised Programme RP15 - 3-Month Rolling Programme for 01 Apr. 2010 to 28 Jun. 2010

	Early bar
	Progress bar
	Critical bar
	Summary bar
	Start milestone point
	Finish milestone point

Act ID	Description	Orig Dur	Total Float	Percent Complete	Early Start	Early Finish	2006 2007 2008 2009 2010																							
							E J F M A M J J A S O N D		J F M A M J J A S O N D		J F M A M J J A S O N D		J F M A M J J A S O N D		J F M A M J J A S O N D															
S4PS1200	Pressure Testing to Twin Rising Main DN700	12	0	0	10MAY10	22MAY10	■ Pressure Test																							
Section 5 - Sewers & RM in Portion E																														
Portion E																														
Preliminaries																														
S5EA1300	Non Work Period 01 Nov 08 - 31 Mar 09	121	0	98	01NOV08 A	02APR10	Non Work Period																							
Section 6 - Sewers in Portion J																														
Portion J																														
Drainage and Ducts																														
Trench Method																														
S6JEA1000	DN500 Pipe & Manhole (C1 - D2) (Deleted SA2)	0		100	02JAN10 A	09APR10 A	DN500 Pipe & M																							
Trenchless Method																														
S6JEB1300	CCTV Inspection of Pipeline	2	0	0	31MAR10	01APR10	CCTV Inspection																							
Geotechnical works																														
S6JP1000	Monitoring of Instruments	1152	0	98	21APR06 A	27APR10	Monitoring of I																							
Section 8 - Preservation and Protection of Trees																														
All Portions																														
Landscape Softworks and Establishment Works																														
S8QR1100	Preservation & Protection of Preserved Trees	1192	0	88	29JUL06 A	16SEP10	P																							
Decontamination Works																														
Portion F																														
Decontamination																														
S9FU1000	Decontamination Works	48	0	95	28AUG09 A	01APR10	Decontamination																							

Start date	19DEC05
Finish date	16SEP10
Data date	31MAR10
Page number	4A
Project name	RP15
© Primavera Systems, Inc.	

Leader Civil Engineering Corp. Ltd.
DSD Contract No. DC/2005/02
Revised Programme RP15 - 3-Month Rolling Programme for 01 Apr. 2010 to 28 Jun. 2010

	Early bar
	Progress bar
	Critical bar
	Summary bar
	Start milestone point
	Finish milestone point


ANNEX D

PHOTOGRAPHICAL RECORDS – NOISE BARRIER ON-SITE



ANNEX E

LOCATIONS OF MONITORING STATIONS

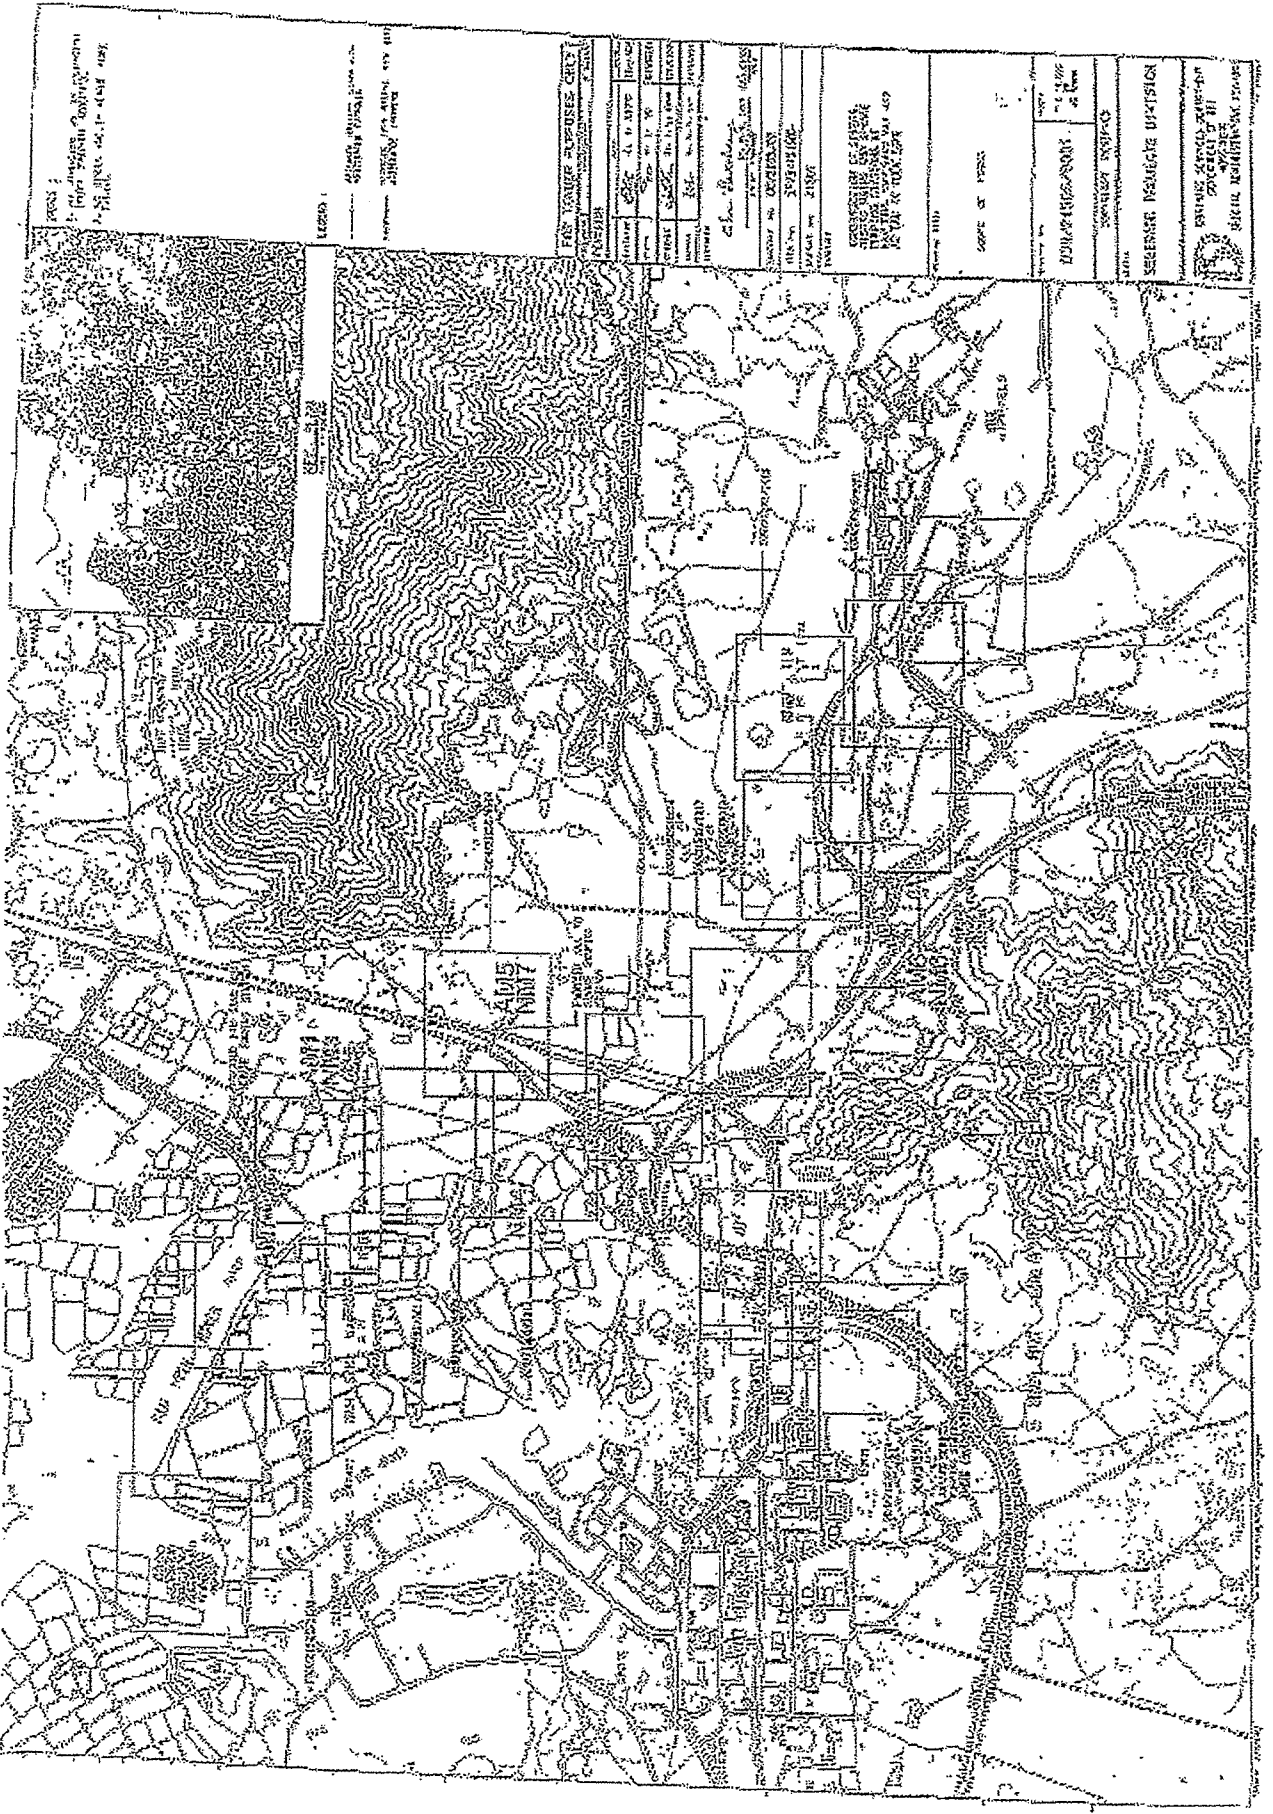

1:50,000
 1:50,000
 1:50,000
 1:50,000
 1:50,000

1:50,000
 1:50,000
 1:50,000
 1:50,000
 1:50,000

1:50,000
 1:50,000
 1:50,000
 1:50,000
 1:50,000


PERMANENT PURPOSES ONLY

CLASSIFICATION	DESCRIPTION
1	...
2	...
3	...
4	...
5	...
6	...
7	...
8	...
9	...
10	...
11	...
12	...
13	...
14	...
15	...
16	...
17	...
18	...
19	...
20	...
21	...
22	...
23	...
24	...
25	...
26	...
27	...
28	...
29	...
30	...
31	...
32	...
33	...
34	...
35	...
36	...
37	...
38	...
39	...
40	...
41	...
42	...
43	...
44	...
45	...
46	...
47	...
48	...
49	...
50	...

1:50,000
 1:50,000
 1:50,000
 1:50,000
 1:50,000

1:50,000
 1:50,000
 1:50,000
 1:50,000
 1:50,000

1:50,000
 1:50,000
 1:50,000
 1:50,000
 1:50,000

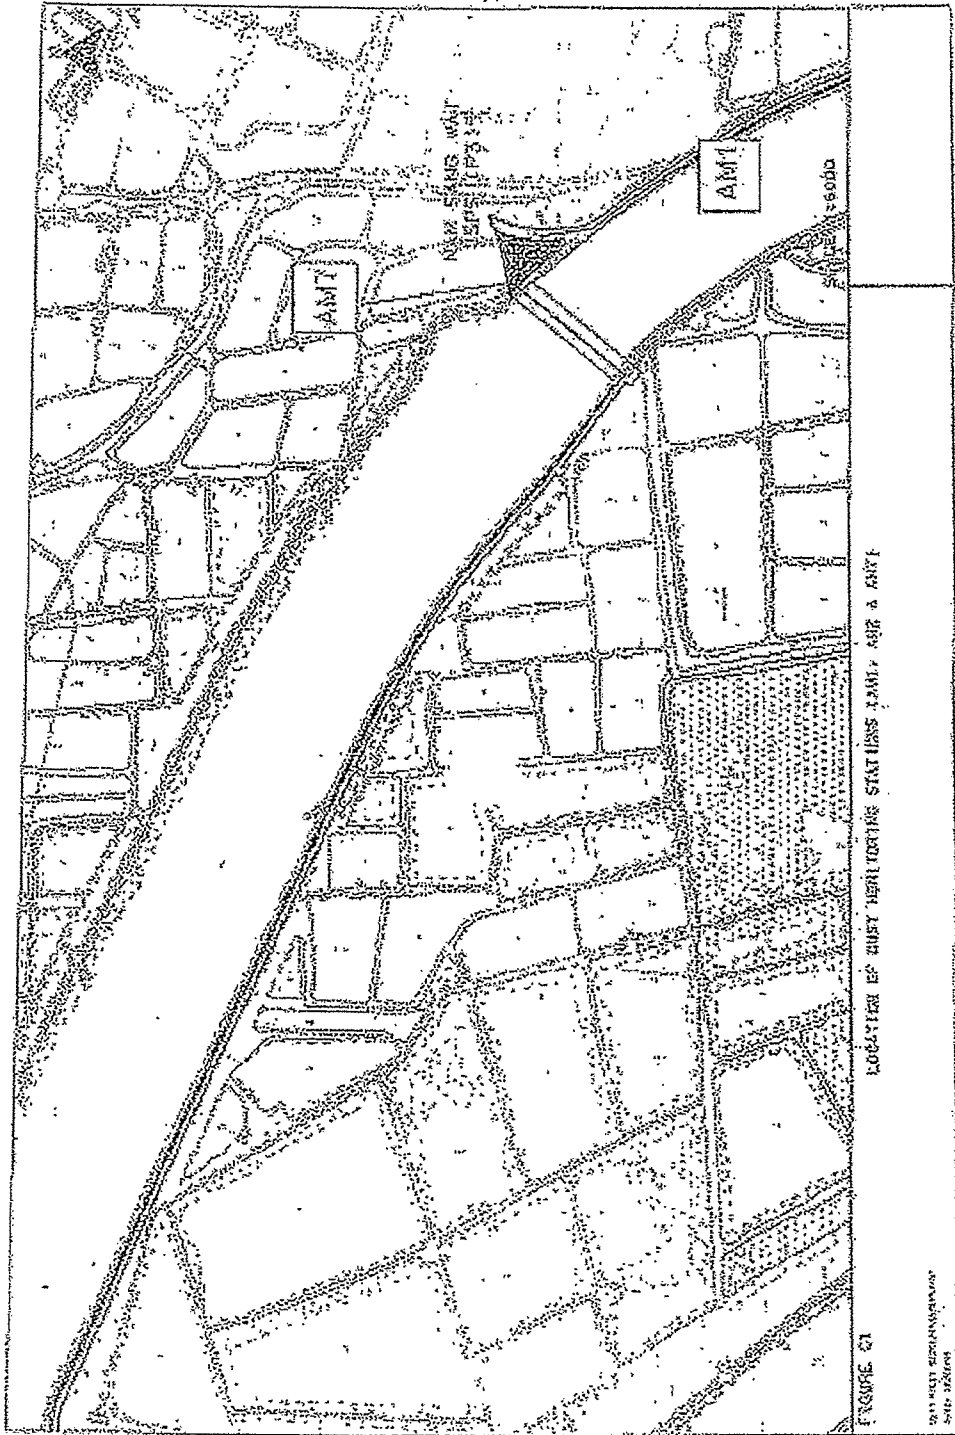

LOCATION OF CHRY HERITORS STATISS JAMI & AIR A AIRT

FIGURE 61


BY THE SURVEYOR GENERAL
OF THE DISTRICT OF COLUMBIA



FIGURE OF BEST MONITORING STATION LAYOUT

FIGURE 62


Scale: 1/4" = 1'-0"
Sheet No. 62

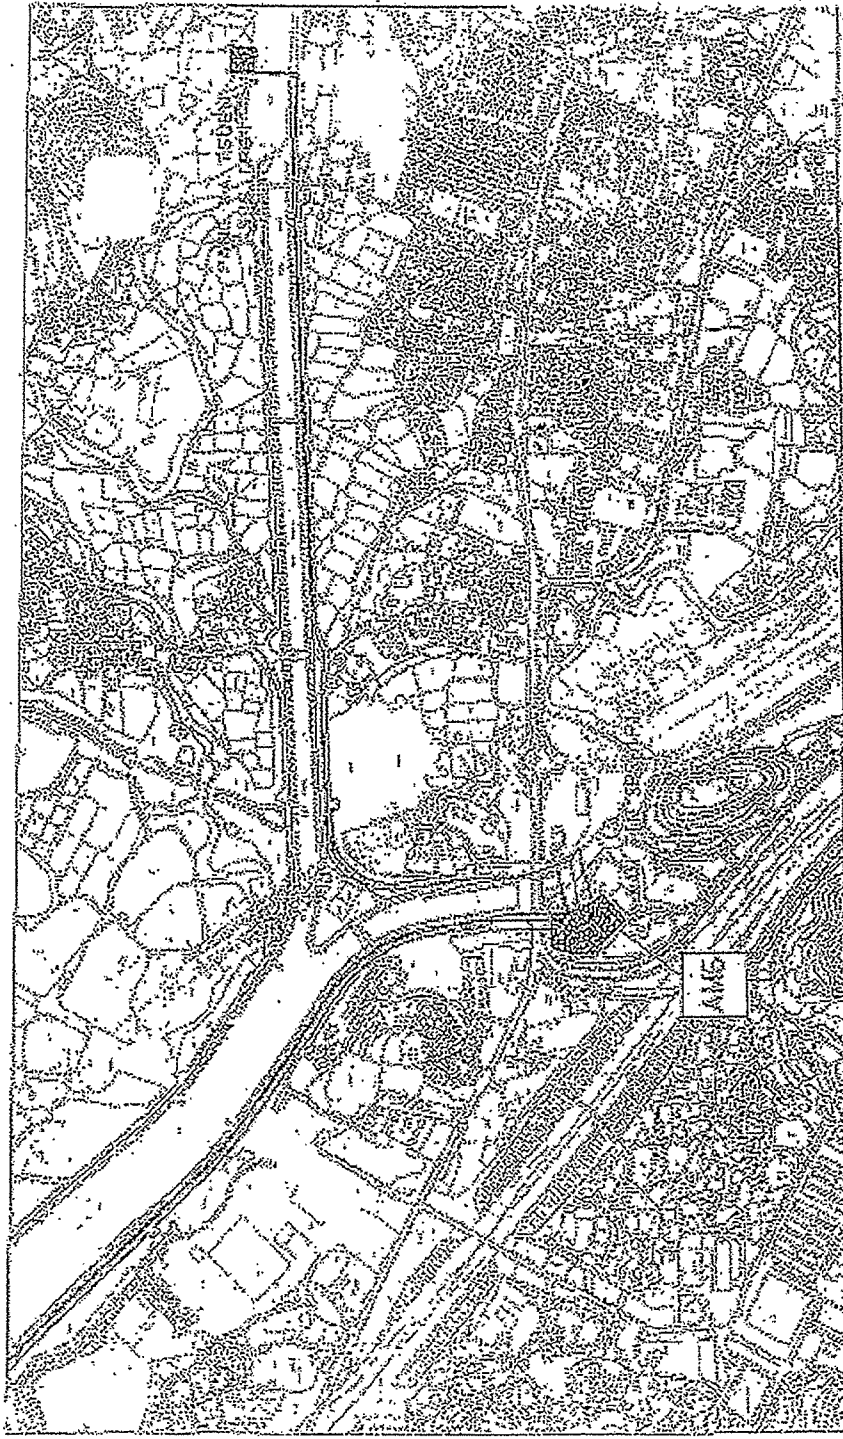

LOCATION OF BEST MONITORING STATIONS (AMC, AMS & AMOS)

FIGURE 50

AMERICAN OVERSEAS AIRWAYS CORPORATION
1960-1961

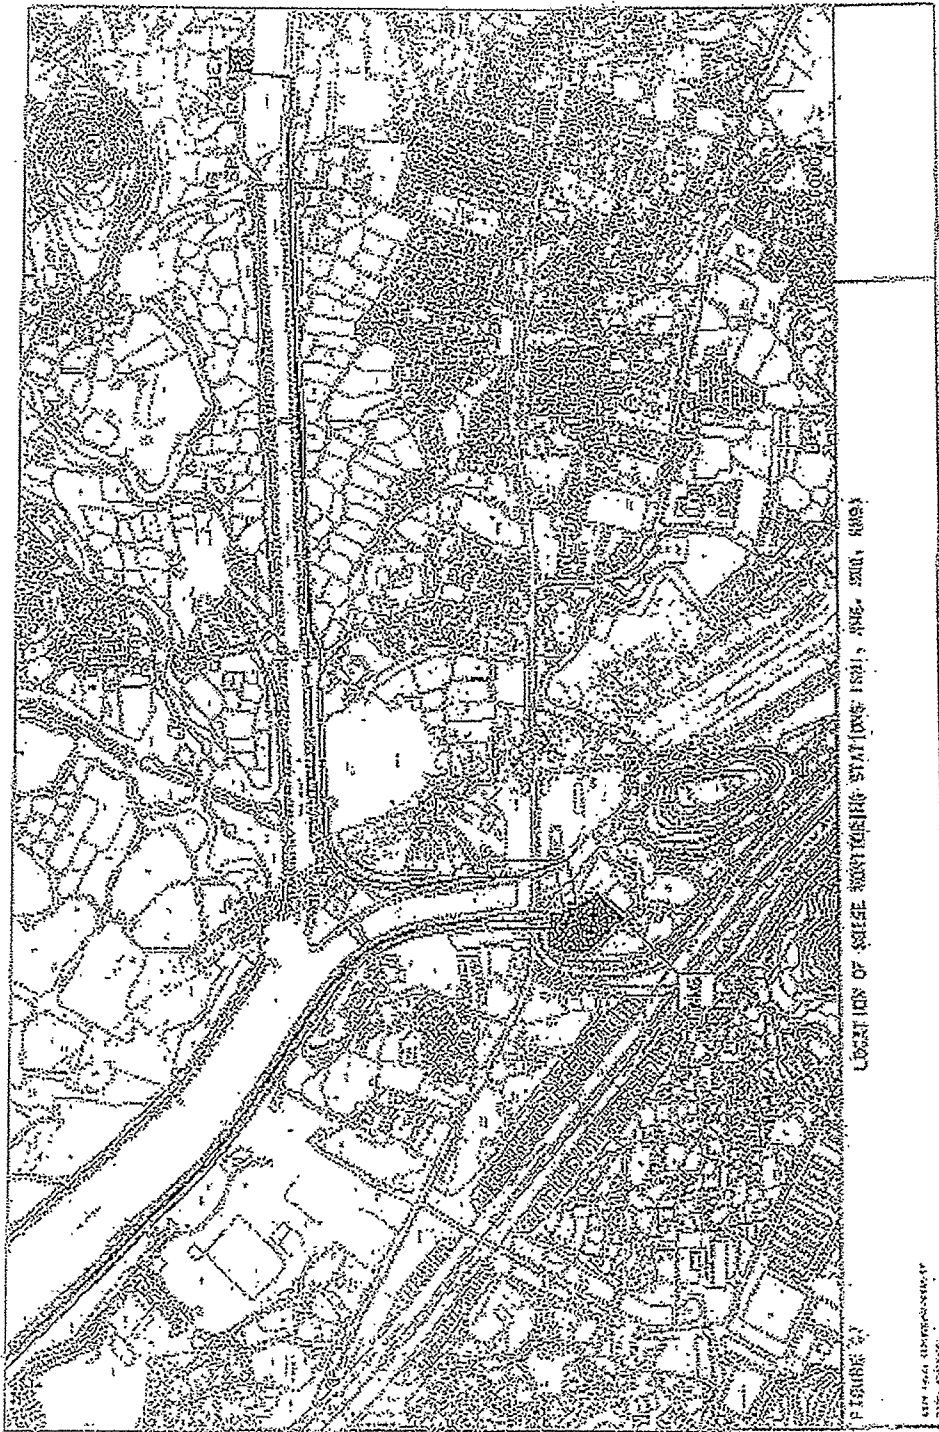

LOCATIONS OF SILENT HOISTING STATIONS 1931, 1932, 1933

FIGURE 4

NEW YORK UNIVERSITY

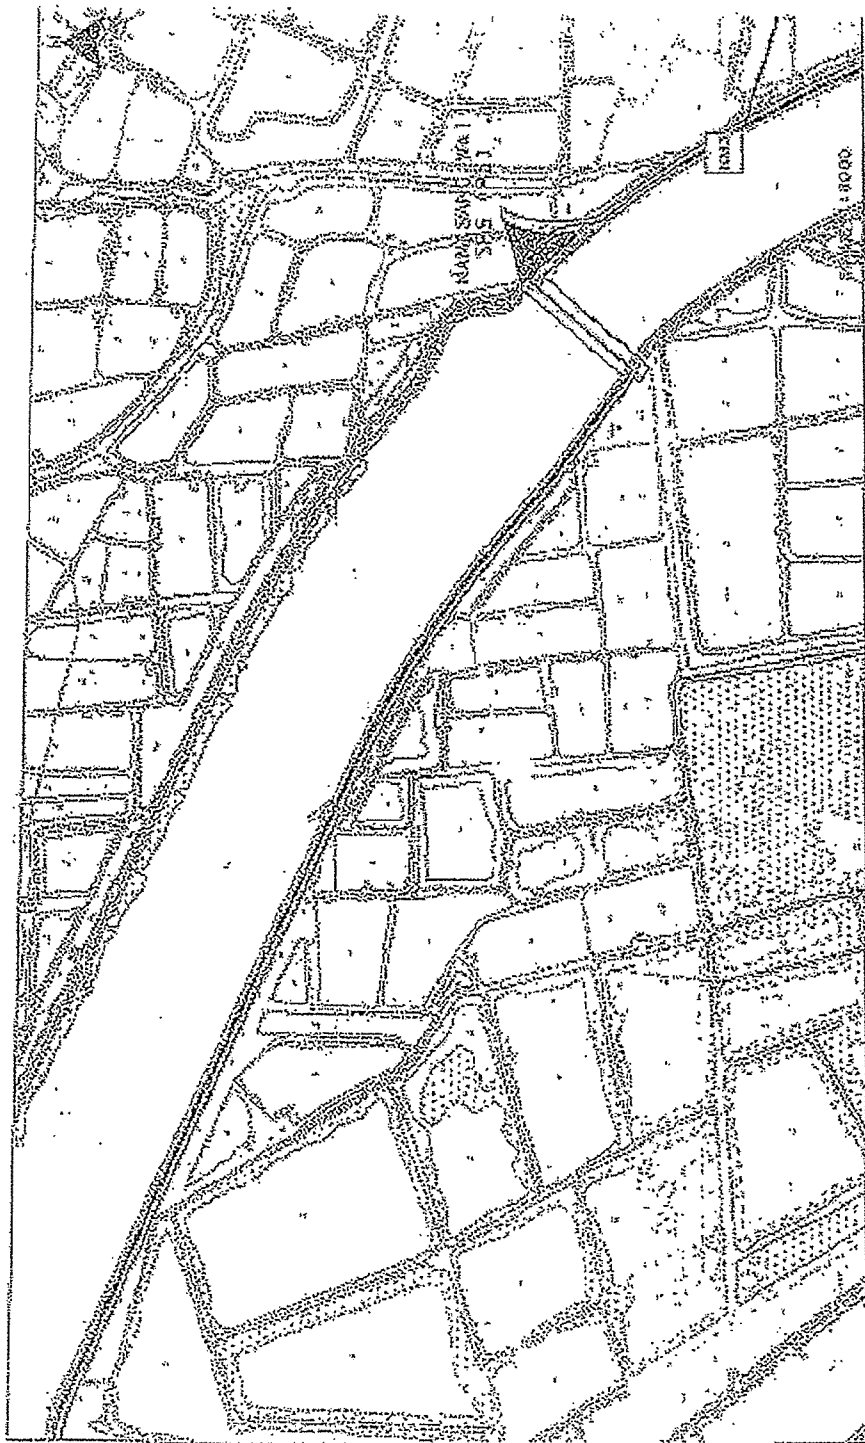


FIGURE 10

LOCATION OF HOUSE FURNITURE STATIONS (IND. 1871)

REPRODUCED FROM THE
 1871 CENSUS



LOCATION OF NOISE MONITORING STATIONS FROM MAP 2

SCALE 1:500

BY: [unreadable]
DATE: [unreadable]

ANNEX F

EVENT AND ACTION PLAN

Monthly EM&A Report for April 2010 (No. 49) (Designated Elements)

Event and Action Plan for Construction Phase Air Quality

EVENT	ACTION			
	ET Leader	IEC	Engineer	Contractor
<i>Action Level</i>				
Exceedance for one sample	<ol style="list-style-type: none"> Identify source (s) of exceedance and inform IEC, Contractor and Engineer Repeat dust measurements to confirm findings Increase monitoring frequency to daily Assess efficacy of remedial measures and keep the Contractor, IEC, and Engineer informed 	<ol style="list-style-type: none"> Check monitoring data submitted by ET Check monitoring data trends and Contractors working methods Check and confirm Contractors proposed remedial actions and working methods are appropriate 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing Remind the Contractor of his contractual obligations and review the Contractor's working methods Discuss remedial actions with the Contractor and IEC Inform complainant of actions taken, if necessary 	<ol style="list-style-type: none"> Rectify any unacceptable practice Liaise with Engineer and IEC to develop appropriate remedial measures to reduce dust impact Amend working methods and remedial proposals if required by the Engineer or IEC Implement the agreed remedial actions upon instruction from the Engineer and IEC
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> Identify source (s) of exceedance and inform IEC, Contractor and Engineer Repeat measurements to confirm findings Increase the monitoring frequency to daily to assess the efficacy of remedial measures and keep the Contractor informed Discuss remedial actions with IEC and Contractor If exceedance continues, arrange meeting with Engineer, IEC and Contractor to review working practices and identify further remedial actions If exceedance stops, inform the Contractor and cease additional monitoring 	<ol style="list-style-type: none"> Check monitoring data submitted by ET Check monitoring data trends and Contractors working methods Discuss with Contractor and Engineer on possible remedial measures Check and confirm Contractors proposed remedial measures are appropriate Determine the efficacy of remedial actions and keep the Engineer informed 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing Remind the Contractor of his contractual obligations and review the Contractor's working methods Discuss remedial actions with the Contractor and IEC Ensure remedial measures are properly implemented Inform complainant of actions taken, if necessary. 	<ol style="list-style-type: none"> Rectify any unacceptable practice, if possible Submit proposals for remedial actions to Engineer and IEC within three working days of notification Discuss and amend remedial actions, if required, by the Engineer and IEC Implement the remedial action (s) immediately upon instruction from the Engineer Discuss with Engineer and IEC, to optimise the effectiveness of the agreed remedial actions

Monthly EM&A Report for April 2010 (No. 49) (Designated Elements)

Event and Action Plan for Construction Phase Air Quality

EVENT	ACTION			
	ET Leader	IEC	Engineer	Contractor
<i>Limit Level</i>				
Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source (s) of exceedance and inform IEC, Contractor and Engineer 2. Repeat dust measurements to confirm findings 3. Increase monitoring frequency to daily 4. Assess efficacy of remedial measures and keep the Contractor, IEC, Engineer and EPD informed 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET 2. Check monitoring data trends and Contractors working methods 3. Check and confirm Contractors proposed remedial actions and working methods are appropriate 4. Check and confirm Contractors proposed remedial measures are appropriate 5. Determine the efficacy of remedial actions and keep the Engineer informed 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing 2. Remind the Contractor of his contractual obligations and review the Contractor's working methods 3. Discuss remedial actions with the Contractor and IEC, 4. Ensure remedial measures are properly implemented 5. Inform complainant of actions taken, if necessary. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance 2. Submit proposals for remedial actions to Engineer and IEC within three working days of notification 3. Discuss and amend remedial actions, if required, by the Engineer and IEC 4. Implement the remedial action (s) immediately upon instruction from the Engineer 5. Discuss with Engineer and IEC, to optimise the effectiveness of the agreed remedial actions
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source (s) of exceedance and inform IEC, Contractor and Engineer 2. Repeat measurements to confirm findings 3. Increase the monitoring frequency to daily to assess the efficacy of remedial measures and keep the Contractor informed 4. Discuss remedial actions with IEC and Contractor 5. If exceedance continues, arrange meeting with Engineer, IEC and Contractor to review working practices and identify further remedial actions 6. If exceedance stops, inform the Contractor and cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss with Contractor and Engineer on possible remedial measures 2. Check and confirm Contractors proposed remedial measures are appropriate 3. Determine the efficacy of remedial actions and keep the Engineer informed 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of exceedance in writing 2. Remind the Contractor of his contractual obligations and review the Contractor's working methods 3. Discuss remedial actions with the Contractor and IEC 4. Ensure remedial measures are properly implemented 5. If exceedance continues, instruct the Contractor to stop the relevant portion of work until the exceedance is abated 6. Inform complainant of actions taken, if necessary. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice, if possible 2. Submit proposals for remedial actions to Engineer and IEC within three working days of notification 3. Discuss and amend remedial actions, if required, by the Engineer and IEC 4. Implement the remedial action (s) immediately upon instruction from the Engineer 5. Discuss with Engineer and IEC, to optimise the effectiveness of the agreed remedial actions

Monthly EM&A Report for April 2010 (No. 49) (Designated Elements)

Event and Action Plan for Construction Noise				
EVENT	ACTION			
	ET Leader	IEC	Engineer	Contractor
<i>Limit Level</i>				
Exceedance for one sample	<ol style="list-style-type: none"> Identify source (s) of exceedance and inform IEC, Contractor and Engineer Repeat dust measurements to confirm findings If repeat measurements confirm exceedance, increase monitoring frequency to daily Assess efficacy of remedial measures and keep the Contractor, IEC, and Engineer informed If exceedance stops, inform Contractor and cease additional noise monitoring 	<ol style="list-style-type: none"> Check monitoring data submitted by ET Check monitoring data trends and Contractors working methods Check and confirm Contractors proposed remedial actions and working methods are appropriate 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing Remind the Contractor of his contractual obligations and review the Contractor's working methods Discuss remedial actions with the Contractor and IEC Inform complainant of actions taken, if necessary 	<ol style="list-style-type: none"> Rectify any unacceptable practice Liaise with Engineer and IEC to develop appropriate remedial measures to reduce noise impact Amend working methods and remedial proposals if required by the Engineer or IEC Implement the agreed remedial actions upon instruction from the Engineer and IEC
Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> Identify source (s) of exceedance and inform IEC, Contractor and Engineer Repeat measurements to confirm findings Increase the monitoring frequency to daily Discuss remedial actions with IEC, Engineer and the EPD Assess the efficacy of remedial measures and keep the Contractor informed If exceedance continues, arrange meeting with Engineer, IEC and Contractor to review working practices and identify further remedial actions If exceedance stops, inform the Contractor and cease additional monitoring. 	<ol style="list-style-type: none"> Check monitoring data submitted by ET Check monitoring data trends and Contractors working methods Discuss with Contractor and Engineer on possible remedial measures Check and confirm Contractors proposed remedial measures are appropriate Determine the efficacy of remedial actions and keep the Engineer informed 	<ol style="list-style-type: none"> Confirm receipt of notification of exceedance in writing Remind the Contractor of his contractual obligations and review the Contractor's working methods Discuss remedial actions with the Contractor and IEC Ensure remedial measures are properly implemented If exceedance continues, instruct the Contractor to stop the relevant portion of work until the exceedance is abated Inform complainant of actions taken, if necessary. 	<ol style="list-style-type: none"> Rectify any unacceptable practice, if possible Submit proposals for remedial actions to Engineer and IEC within three working days of notification Discuss and amend remedial actions, if required, by the Engineer and IEC Implement the remedial action (s) immediately upon instruction from the Engineer Discuss with Engineer and IEC, to optimise the effectiveness of the agreed remedial actions Stop the relevant portion of work as determined by the Engineer until the exceedance is abated

ANNEX G

MITIGATION IMPLEMENTATION SCHEDULE

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
CONSTRUCTION PHASE										
AIR QUALITY - Construction Phase										
		The following measures are enforceable under the <i>Air Pollution Control (Construction Dust) Regulations</i>								
3.5	A1	<p>Site boundary and entrance</p> <ul style="list-style-type: none"> where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of not less than 2.4 m high from ground level should be provided along the boundaries of the seven pumping stations sites and the works area where the Engineer's site office and the Contractor's site office erected; 	To prevent access to the site and control potential dust impacts from construction works.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Part III, Clause 13 (c), Air Pollution Control (Construction Dust) Regulations</i>
3.5	A2	<p>Access Road</p> <ul style="list-style-type: none"> the portion of any road leading only to a construction site that is within 30 m of a discernible or designated vehicle entrance or exit should be kept clear of dusty materials; 	To control potential dust impacts from vehicle movements.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Part III, Clause 14, (b), Air Pollution Control (Construction Dust) Regulations</i>
3.5	A3	<p>Stockpiling of Dusty Materials</p> <ul style="list-style-type: none"> any stockpile of dusty materials should be either covered entirely by impervious sheeting and placed in an area sheltered on the top and the 3 sides or sprayed with water so as to maintain the entire surface wet; 	To control potential dust impacts during excavation and stockpiling activities.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Part IV, Clause 18, (a, b & c), Air Pollution Control (Construction Dust) Regulations</i>
3.5	A4	<p>Loading, unloading or transfer of dusty materials</p> <ul style="list-style-type: none"> all dusty materials should be sprayed with water or a dust suppression chemical immediately prior to any loading and unloading so as to maintain the dusty materials wet; 	To control potential dust impacts during material handling and truck movements.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Part IV, Clause 19, Air Pollution Control (Construction Dust) Regulations</i>
3.5	A5	<p>Use of vehicles</p> <ul style="list-style-type: none"> every vehicle should be washed to remove any dusty materials from its body and wheels immediately before leaving a construction site; 	To control potential dust impacts from vehicle movements.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Part IV, Clause 21, (1), Air Pollution Control (Construction</i>

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
3.5	A6	<ul style="list-style-type: none"> where a vehicle leaving a construction site is carrying a load of dusty materials, the load should be covered entirely by clean impervious sheeting to ensure that the dusty materials do not leak from the vehicle; 	To control potential dust impacts during material transportation.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Dust) Regulations Part IV, Clause 21, (2), Air Pollution Control (Construction Dust) Regulations</i>
3.5	A7	<p>Power-driven drilling, and cutting</p> <ul style="list-style-type: none"> water should be continuously sprayed on the surface where any mechanical breaking operation that causes dust emission is carried out, unless the process is accompanied by the operation of an effective dusty extraction and filtering device; 	To control potential dust impacts during mechanical breaking.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Part IV, Clause 22, Air Pollution Control (Construction Dust) Regulations</i>
3.5	A8	<p>Excavation and earth moving</p> <ul style="list-style-type: none"> the working area of excavation should be sprayed with water immediately before, during and immediately after the operation so as to maintain the entire surface wet; 	To control potential dust impacts arising from excavation works.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Part IV, Clause 24, Air Pollution Control (Construction Dust) Regulations</i>
3.5	A9	<p>Construction of the superstructure of a building</p> <ul style="list-style-type: none"> where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the round floor level of the SPS, or if a canopy is provided at the first floor level, from the first floor level, up to the highest level of the scaffolding; and 	To control potential dust impacts from SPS building construction works.	Full duration of SPS construction contract.	The Contractor		✓			<i>Part I, Clause 6, (a), Air Pollution Control (Construction Dust) Regulations</i>
3.5	A10	<ul style="list-style-type: none"> any skip hoist for material transport should be totally enclosed by the impervious sheeting. 	To control potential dust impacts during material transportation.	Full duration of SPS construction contract.	The Contractor		✓			<i>Part I, Clause 6, (b), Air Pollution Control (Construction Dust) Regulations</i>

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
		NOISE - Construction Phase								
4.7.1	B1	<p>General Site Clearance – Demolition Works</p> <ul style="list-style-type: none"> Use of quiet PME which meet the SWLs taken from British Standard, <i>Noise and Vibration Control on Construction Open Sites, BS 5228: Part 1: 1997</i> (Examples of these PME are shown in Table F2), 	To control potential noise impacts during site clearance and demolition works	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Annex 5 of EIAO-TM</i>
4.7.1	B2	<p>Construction of Sewage Pumping Stations P1, P2 & P3</p> <ul style="list-style-type: none"> Use of quiet PME which meet the SWLs taken from British Standard, <i>Noise and Vibration Control on Construction Open Sites, BS 5228: Part 1: 1997</i>, Adoption of temporary noise barrier, in the form of a site hoarding (with a superficial density of at least 20kg/m², with no substantial gaps), along the site boundary of the pumping station sites. 	To minimise potential noise impacts arising during the construction of P1, P2 & P3	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Annex 5 of EIAO-TM</i>
4.7.1	B3	<p>Sewers and Rising Mains using Open Trench Method</p> <ul style="list-style-type: none"> Use of quiet PME which meet the SWLs taken from British Standard, <i>Noise and Vibration Control on Construction Open Sites, BS 5228: Part 1: 1997</i>, 	To minimise potential noise impacts arising during the construction of P1, P2 & P3	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Annex 5 of EIAO-TM</i>
4.7.1	B4	<ul style="list-style-type: none"> Use of handheld breakers for all initial road opening activities, when breaking tarmac/concrete road surface to a depth of 300mm or when granular material is reached. 	To control potential noise impacts during excavation works.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Annex 5 of EIAO-TM</i>
4.7.1	B5	<ul style="list-style-type: none"> Use of handheld breakers for all initial road opening activities, when breaking tarmac/concrete road surface to a depth of 300mm or when granular material is reached. 	To control potential noise impacts during road opening activities.	Where there are NSRs located within 50m of the line of sight. Throughout the full duration of the road opening activities.	The Contractor		✓			<i>Annex 5 of EIAO-TM</i>
4.7.1	B5	<ul style="list-style-type: none"> Use of movable noise barriers or 3 sided enclosures for all initial road opening activities 	To control potential noise impacts during road opening	Where there are NSRs located within 50m of the	The Contractor		✓			<i>Annex 5 of EIAO-TM</i>

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
4.7.1	B6	enclosures for all initial road opening activities (breaking tarmac/concrete road surface to a depth of 300mm or when granular material is reached), where there are NSRs located within 50m of the line of sight from the works area. Sewers and Rising Mains using Pipe Jacking Method • Use of quiet PME which meet the SWLs taken from British Standard, <i>Noise and Vibration Control on Construction Open Sites, BS 5228: Part 1: 1997,</i>	activities. To control potential noise impacts from PME during construction works	line of sight. Throughout the full duration of the road opening activities. Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Annex 5 of EIAO-TM</i>
4.7.1	B7	Road Pavement and Finishes • Use of quiet PME which meet the SWLs taken from British Standard, <i>Noise and Vibration Control on Construction Open Sites, BS 5228: Part 1: 1997,</i>	To control potential noise impacts from PME during pavement and finish works	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			<i>Annex 5 of EIAO-TM</i>
		WATER QUALITY - Construction Phase No water quality monitoring is required under this study.								
6.6.2	D1	WASTE - Construction Phase The Contractor shall obtain the necessary waste disposal permits from the appropriate authorities for the disposal of chemical and C&D waste, • Chemical Waste Producer and Chemical Waste Disposal Licence (<i>Waste Disposal (Chemical Waste) (General) Regulations</i>); and • Dumping Licence (<i>Land (Miscellaneous Provisions) Ordinance (Cap 28)</i>)	To monitor the collection, handling and disposal of chemical waste and C&D waste, and in compliance with relevant Hong Kong Standards and Regulations.	Site wide and throughout the full duration of the construction contract.	The Contractor	✓	✓			<i>Waste Disposal Ordinance (Cap 354), Waste Disposal (Chemical Waste)(General) Regulation (Cap 354), the Land (Miscellaneous Provisions) Ordinance (Cap 28)</i>

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
6.6.2	D2	<p>Chemical Waste Chemical waste that is produced, as defined by Schedule 1 of the <i>Waste Disposal (Chemical Waste) (General) Regulation</i>, should be handled in accordance with the regulations and Code of Practice on the Packaging, Handling and Storage of Chemical Wastes as follows. All chemical waste producers should be registered with the EPD.</p>	To control the handling, storage and disposal of chemical waste, in order to minimise potential spillages/leakages and human health and environmental impacts.	To be implemented at all worksites throughout the full duration of the construction phase.	The Contractor		✓			<i>Part II, (6) Waste Disposal (Chemical Waste) (General) Regulation</i>
6.6.2	D3	<p>Storage, Packaging and Labelling of Chemical Waste Containers used for storage of chemical wastes should:</p> <ul style="list-style-type: none"> be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; have a capacity of less than 450 L unless the specifications have been approved by the EPD; and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the Regulations. 	To ensure the proper storage, packaging and labelling of chemical waste in accordance with the Regulations.	To be implemented at all worksites throughout the full duration of the construction phase.	The Contractor		✓			<i>Part IV, (9, 10, 11 & 12) Waste Disposal (Chemical Waste) (General) Regulation</i>
6.6.2	D4	<p>Storage of chemical waste The storage area for chemical wastes should:</p> <ul style="list-style-type: none"> be clearly labelled and used solely for the storage of chemical waste; be enclosed on at least 3 sides; have an impermeable floor and bunding, of capacity to accommodate 110% of the volume of the largest container or 20% by volume of the chemical waste stored in that area, whichever is the greatest; have adequate ventilation; be covered to prevent rainfall entering (water collected within the bund must be tested and disposed as chemical waste, if necessary); and be arranged so that incompatible materials are 	To ensure the proper storage of chemical waste in accordance with the Regulations.	To be implemented at all worksites throughout the full duration of the construction phase.	The Contractor		✓			<i>Part IV, (13,14, 15, 16, 17, & 18) Waste Disposal (Chemical Waste) (General) Regulation</i>

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
		adequately separate								
6.6.2	D5	<p>Disposal of chemical waste</p> <ul style="list-style-type: none"> The Contractor should ensure that the disposal of chemical waste is via a licensed Waste Collector and in accordance with the <i>Waste Disposal (Chemical Waste) (General) Regulations</i>. <p><i>Management of Waste Disposal</i> A trip-ticket system should be established which monitors the disposal of C&DM and solid wastes at public filling facilities and landfills and to control fly-tipping, in accordance with <i>Land (Miscellaneous Provisions) Ordinance (Cap28)</i> and the <i>Works Bureau Technical Circular No. 5/99</i>.</p>	<p>To control the disposal of chemical waste in accordance with the Regulations.</p>	To be implemented at all worksites throughout the full duration of the construction phase.	The Contractor		✓			<i>Part IV, (20 -25) Waste Disposal (Chemical Waste) (General) Regulation</i>
		<p>LAND CONTAMINATION- Construction Phase</p> <p>A revised CAP should be submitted to the EPD for approval before the commencement of the construction works. Following receipt of the EPD's approval, the CAP shall be implemented and the findings of the investigations will be reported in the Contaminated Assessment Report (CAR), before ground disturbance is allowed at the concerned sites. If land contamination is confirmed, a Remediation Action Plan (RAP) shall be prepared, and both the CAR and the RAP shall be submitted as a combined report to the EPD for approval before disturbing the ground of the concerned sites. If applicable and required in consultation with the</p>	<p>To monitor the disposal of C&DM and solid wastes at public filling facilities and landfills and to control fly-tipping.</p>	To be implemented at all worksites throughout the full duration of the construction phase.	The Engineer/ Contractor		✓			<i>Land (Miscellaneous Provisions) Ordinance (Cap 295) and Works Bureau Technical Circular No. 5/99.</i>
7.5.6	E1	<p>A revised CAP should be submitted to the EPD for approval before the commencement of the construction works. Following receipt of the EPD's approval, the CAP shall be implemented and the findings of the investigations will be reported in the Contaminated Assessment Report (CAR), before ground disturbance is allowed at the concerned sites. If land contamination is confirmed, a Remediation Action Plan (RAP) shall be prepared, and both the CAR and the RAP shall be submitted as a combined report to the EPD for approval before disturbing the ground of the concerned sites. If applicable and required in consultation with the</p>	<p>To determine the presence of soil and groundwater contamination and remedy any potential concerns to acceptable levels.</p>	To be implemented before the commencement of the construction works.	To be Implemented by DSD or their sub-consultants at the Detailed Design Stage, depending upon when site access can be gained.	✓				<i>EIAO TM Annex 19/3.1.1 & 3.1.2</i>

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
		EPD, the contaminated site(s) shall be remediated in accordance with the approved CAR/RAP.								
8.7.1	F1	<p>ECOLOGY - Construction Phase Mitigation Measures Adopted - Avoidance Construction activities shall be prohibited during the winter season (November to March) along the section of the proposed sewerage alignment, which fall within the Deep Bay Wetland Conservation Area and the Deep Bay Wetland Buffer Area (WCA and WBA) and close to the locations of ecologically sensitive species (including Intermediate Egret, Black-faced Spoonbill, Buzzard, Imperial Eagle and Avocet). (See Figure 8.7a attached). Regular site inspections (at least twice a month) should be conducted by the Environmental Team during the winter season (November to March) to ensure proper implementation of this restriction</p>	To schedule construction works in order to minimise potential impacts to winter visiting birds. To be confirmed by regular site inspections.	At identified location (<i>Figure 8.7a</i>) for the full duration of the construction contract.	The Contractor		✓			
8.7.2	F2	<p>Mitigation Measures Adopted - Minimisation Pipe jacking method should be used instead of dredging where sewers and rising mains cross over existing MDC within the WCA and WBA.</p>	To minimise potential construction noise impacts to ecological sensitive receivers within the WCA/WBA.	For the full duration of the construction contract.	The Contractor		✓			
8.7.2	F4	<p>Regular inspections (at least twice a month) should be conducted by the ET during the winter season (November to March) for the remaining sections of the proposed sewerage alignment (including parts of S4, S5 and S6) within the WCA and WBA, where construction activities cannot be rescheduled.</p> <p>The site inspections shall check and report the number of workfronts and implementation of</p>	To schedule noisy construction activities to minimise potential impacts to winter visiting birds.	Work fronts other than identified sections within WBA & WCA (see <i>Figure 8.7a</i> attached) throughout the full duration of the construction contract.	The Contractor		✓			

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
8.7.3	F5	mitigation measures (i.e. erection of movable noise barriers with a suitable footing along the sites) in the monthly EM&A reports. Mitigation Measures Adopted Quietened construction plant and equipment (as shown in <i>Table F2</i>) should be used for the construction of pumping stations (P3 and P2) and sewerage alignment (S4, S5 and S6) located within the WCA and WBA.	Quiet construction plant shall minimise potential noise impacts to the wildlife, particularly rare birds including Black-faced Spoonbill, Buzzard, Hobby, Imperial Eagle, Intermediate Egret, Avocet and Black-eared Kite	At described locations and throughout the full duration of the construction contract.	The Contractor		✓			
8.7.4	F6	Erection of fences along the boundary of pumping station construction sites (P1 to P3) before the commencement of construction works to prevent tipping, vehicle movements, and encroachment of personnel into adjacent areas, and P2 to avoid disturbance to the remaining pond areas (0.7 ha);	To erect fences to prevent encroachment of construction activities onto adjacent areas.	At P1 to P3 for full duration of the construction contract.	The Contractor		✓			
8.7.4	F7	No filling and dumping to the remaining abandoned fishpond at P2.	To avoid disturbance to abandoned fishponds from construction activities and illegal dumping.	At P2 for full duration of the construction contract	The Contractor		✓			
8.7.4	F8	Installation and operation of silt removal facilities at construction sites of P1 to P3. The silt removal facilities should be designed in accordance with Appendix A1 of ProPECC Note PN1/94 Construction Site Drainage. The minimal total combined volume of the silt removal facilities at Nam Sang Wai SPS (P3) should be 15m ³ .	To install silt removal facilities in potentially impact streams and ponds to prevent sedimentation.	At P1 to P3 for full duration of the construction contract.	The Contractor		✓			
8.7.4	F9	No open fires within the site boundary during	To prohibit open fires, thereby	Site wide and throughout	The Contractor		✓			<i>Air Pollution Control</i>

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
8.7.4	F7	construction and provide temporary fire fighting equipment in the work areas. No filling and dumping to the remaining abandoned fishpond at P2.	minimising potential damage to trees and shrubs. To avoid disturbance to abandoned fishponds from construction activities and illegal dumping.	the full duration of the construction contract. At P2 for full duration of the construction contract	The Contractor		✓			(Open Burning) Regulation
8.7.4	F8	Installation and operation of silt removal facilities at construction sites of P1 to P3. The silt removal facilities should be designed in accordance with Appendix A1 of ProPECC Note PN1/94 Construction Site Drainage.	To install silt removal facilities in potentially impact streams and ponds to prevent sedimentation.	At P1 to P3 for full duration of the construction contract.	The Contractor		✓			
8.7.4	F9	No open fires within the site boundary during construction and provide temporary fire fighting equipment in the work areas.	To prohibit open fires, thereby minimising potential damage to trees and shrubs.	Site wide and throughout the full duration of the construction contract.	The Contractor		✓			Air Pollution Control (Open Burning) Regulation
		FISHERIES - Construction Phase No specific mitigation measures are required for inclusion in the EP.								
		CULTURAL HERITAGE – Not Applicable for Package 1A-1T (DC/2005/02)								
		LANDSCAPE AND VISUAL - Construction Phase								
	H1	The site inspections shall check and report the implementation of mitigation measures (i.e. top-soil are reused and new compensatory planting works are carried out immediately after the construction of the civil structure) in the monthly EM&A reports. The first monthly EM&A Report should also report the appearance of the temporary hoarding barriers.	To minimise potential landscape and visual impacts.	To be implemented during the construction phases of the project.	The Contractor		✓			
	H2	Prior to application for an Environmental Permit, a set of landscape plans and building elevations of the proposed pumping stations should be	To minimise potential landscape and visual impacts.	To be implemented during the design and construction phases of the	DSD and The Contractor	✓	✓			

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
		submitted for approval by the EPD. The landscape plans and pumping station elevations should demonstrate that the following elements are considered: <ul style="list-style-type: none"> existing landscape elements (such as mature trees), transplantation of valuable trees, new compensatory planting 		project.						
		<ul style="list-style-type: none"> incorporate information on materials, details and textures so as to be as visually recessive as possible and in a style that fits with the surrounding village buildings. colour should be of low chromatic intensity to reduce the potential contrast between the structures and their background. The external finishing of the Pumping Stations shall be designed in conjunction with the landscape scheme. a minimum screen planting of 3m width and use of trees with a dense canopy of up to 5 m in height subject to constraints such as engineering and land availability. felling of mature trees are kept to a minimum. 								
3.7	I1	<p>EM&A REQUIEMENTS - Construction Phase</p> <p><i>Air Quality</i> Subject to the Environmental Protection Departments (EPDs) agreement, construction phase dust monitoring shall be undertaken at the following locations in accordance with the recommendations of the EIA.</p> <ul style="list-style-type: none"> Worksite boundary facing Scattered house in Nam Sang Wai (AM1); Worksite boundary facing Fung Kat Heung (AM5); Worksite boundary facing Scattered House near Route 3 (AM6); 	Installations of the dust monitoring stations to ensure the action and limit levels are not exceeded.	At specified dust monitoring locations for the duration of the construction works.	To be undertaken by the Environmental Team (ET) and reviewed and audited by the Engineer /DSD		✓			<i>Air Pollution Control (Construction Dust) Regulations</i>

EIA* Ref.	EM&A Ref	Environmental Protection Measures	Objectives of the Recommended Measures & Main Concerns	Location of the measure	Implementation Agent	Implementation Stage**				Relevant Legislation & Guidelines
						Des	C	O	Dec	
4.9.1	I2	<ul style="list-style-type: none"> at any additional locations, where considered necessary, in agreement with EPD. <p><i>Construction Noise</i> Subject to the Environmental Protection Departments (EPDs) agreement, construction phase noise monitoring shall be undertaken at the following locations in accordance with the recommendations of the EIA.</p> <ul style="list-style-type: none"> (NM3) Scattered House in Nam San Wai (D12); (NM4) Scattered House in Nam San Wai (D11); (NM6) Scattered House near Route 3 (D17); (NM7) Fung Kat Heung (D19); and at any additional locations, where considered necessary, in agreement with EPD 	Installations of the noise monitoring stations to ensure the action and limit levels are not exceeded.	At specified noise monitoring locations throughout the duration of the construction works.	To be undertaken by the Environmental Team (ET) and reviewed and audited by the Engineer		✓			<i>Noise Control Ordinance</i>

Des = Design, C = Construction, O = Operation, Dec = Decommissioning


ANNEX H

EQUIPMENT CALIBRATION CERTIFICATES

Equipment Calibration List for Construction of Sewers, Rising Mains & Sewage Pumping Station at Kam Tin, Nam Sang Wai and Au Tau in Yuen Long Project

Items	Aspect	Description of Equipment	Serial No.	Date of Calibration	Date of Next Calibration
1*	Air	Greasby Anderson GMWS2310 High Volume Sampler	0329 (AM1)	26 Apr 10	26 Jun 10
2*		Greasby Anderson GMWS2310 High Volume Sampler	(AM5)	1 Apr 10	1 Jun 10
3*		Greasby Anderson GMWS2310 High Volume Sampler	(AM6)	1 Apr 10	1 Jun 10
4*		Greasby Anderson GMWS2310 High Volume Sampler	1283 (AM7)	26 Apr 10	26 Jun 10
5*	Noise	Bruel & Kjaer 4231 Acoustical Calibrator	2285762	27 Apr 10	27 Apr 11
6*		Bruel & Kjaer 2238 Integrating Sound Level Meter	2326408	27 Apr 10	27 Apr 11

Note: Calibration certificates will only be provided if monitoring equipment is re-calibrated or new.
 * Calibration done in this reporting month, see calibration certificate attached.
 ** Calibration will be done in next reporting month.
 # No power was received, thus equipment could not be re-calibrated.



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C102286

Certificate of Calibration

This is to certify that the equipment

Description : Integrating Sound Level Meter (EQ006)

Manufacturer : Bruel & Kjaer

Model No. : 2238

Serial No. : 2285762

*has been calibrated for the specific items and ranges.
The results are shown in the Calibration Report No. C102286.*

The equipment is supplied by

Co. Name : Action-United Environmental Services and Consulting

*Address : Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.*

Date of Issue : 27 April 2010

Certified by :

K C Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

e/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration using the B & K Acoustic Calibrator 4231, S/N : 2326408 was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C100067
CL281	Multifunction Acoustic Calibrator	DC090052

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L _{AFP}	A	F	94.00	1	94.0	± 0.7

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
50 - 130	L _{AFP}	A	F	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

- 6.2 Time Weighting

- 6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L _{AFP}	A	F	94.00	1	94.0	Ref.
	L _{ASP}		S			94.1	± 0.1
	L _{AIP}		I			94.1	± 0.1

The test equipment used for calibration are traceable to the National Standards as specified in this report. This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration Report

6.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
30 - 110	L _{AFP}	A	F	106.0	Continuous	106.0	Ref.
	L _{AFMax}				200 ms	105.0	-1.0 ± 1.0
	L _{ASP}	S	Continuous		106.0	Ref.	
	L _{ASMax}		500 ms		102.0	-4.1 ± 1.0	

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{AFP}	A	F	94.00	31.5 Hz	55.4	-39.4 ± 1.5
					63 Hz	68.1	-26.2 ± 1.5
					125 Hz	78.0	-16.1 ± 1.0
					250 Hz	85.3	-8.6 ± 1.0
					500 Hz	90.7	-3.2 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	95.1	+1.2 ± 1.0
					4 kHz	95.1	+1.0 ± 1.0
					8 kHz	93.3	-1.1 (+1.5 ; -3.0)
					12.5 kHz	90.0	-4.3 (+3.0 ; -6.0)

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{CFP}	C	F	94.00	31.5 Hz	91.8	-3.0 ± 1.5
					63 Hz	93.5	-0.8 ± 1.5
					125 Hz	93.9	-0.2 ± 1.0
					250 Hz	94.0	0.0 ± 1.0
					500 Hz	93.9	0.0 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	93.8	-0.2 ± 1.0
					4 kHz	93.3	-0.8 ± 1.0
					8 kHz	91.3	-3.0 (+1.5 ; -3.0)
					12.5 kHz	88.0	-6.2 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the National Standards as specified in this report. This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration Report

6.4 Time Averaging

UUT Setting				Applied Value					UUT	IEC 60804
Range (dB)	Mode	Frequency Weighting	Integrating Time	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)	Reading (dB)	Type 1 Spec. (dB)
30 - 110	L _{Acq}	A	10 sec.	4	1	1/10	110.0	100	99.8	± 0.5
			60 sec.			1/10 ²		90	89.8	± 0.5
			5 min.			1/10 ³		80	79.3	± 1.0
						1/10 ⁴		70	69.3	± 1.0


Remarks : - Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :
 - 94 dB : 31.5 Hz - 125 Hz : ± 0.40 dB
 - 250 Hz - 500 Hz : ± 0.30 dB
 - 1 kHz : ± 0.20 dB
 - 2 kHz : ± 0.40 dB
 - 4 kHz : ± 0.50 dB
 - 8 kHz : ± 0.70 dB
 - 12.5 kHz : ± 1.20 dB
 - 104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
 - 114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
 - Burst equivalent level : ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C102285

Certificate of Calibration

This is to certify that the equipment

Description : Acoustical Calibrator (EQ081)

Manufacturer : Bruel & Kjaer

Model No. : 4231

Serial No. : 2326408

*has been calibrated for the specific items and ranges.
The results are shown in the Calibration Report No. C102285.*

The equipment is supplied by

Co. Name : Action-United Environmental Services and Consulting

*Address : Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.*

Date of Issue : 27 April 2010

Certified by :

K.C. Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited


c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C102285

Calibration Report

ITEM TESTED

DESCRIPTION : Acoustical Calibrator (EQ081)
MANUFACTURER : Bruel & Kjaer
MODEL NO. : 4231
SERIAL NO. : 2326408

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$ RELATIVE HUMIDITY : $(55 \pm 20)\%$
LINE VOLTAGE : ---

TEST SPECIFICATIONS

Calibration check

DATE OF TEST : 26 April 2010

JOB NO. : IC10-0951

TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Precision Measurement Ltd., UK
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested by :


W L Lai

Date : 27 April 2010

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Page 1 of 2

Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours before the commencement of the test.
2. The results presented are the mean of 3 measurements at each calibration point.
3. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
TST150A	Measuring Amplifier	C101008
CL130	Universal Counter	C093122
CL281	Multifunction Acoustic Calibrator	DC090052

4. Test procedure : MA100N.

5. Results :

- 5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.0		

- 5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : - The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Nam Sang Wai	Date of Calibration: 26-Apr-10
Location ID : AM 7 (Designated)	Next Calibration Date: 26-Jun-10
Serial No: 1283	Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa)	1016.8	Corrected Pressure (mm Hg)	762.6
Temperature (°C)	21.6	Temperature (K)	295

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.01546
Model->	515N	Qstd Intercept ->	-0.02851
Serial # ->	0285		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.1	5.1	10.2	1.611	48	48.64	Slope = 37.3349 Intercept = -11.8290 Corr. coeff. = 0.9993
13	4.2	4.2	8.4	1.463	42	42.56	
10	3	3	6	1.239	34	34.45	
7	2.1	2.1	4.2	1.039	26	26.35	
5	1.3	1.3	2.6	0.820	19	19.25	

Calculations :


$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$
 $IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$

 Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$

 m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

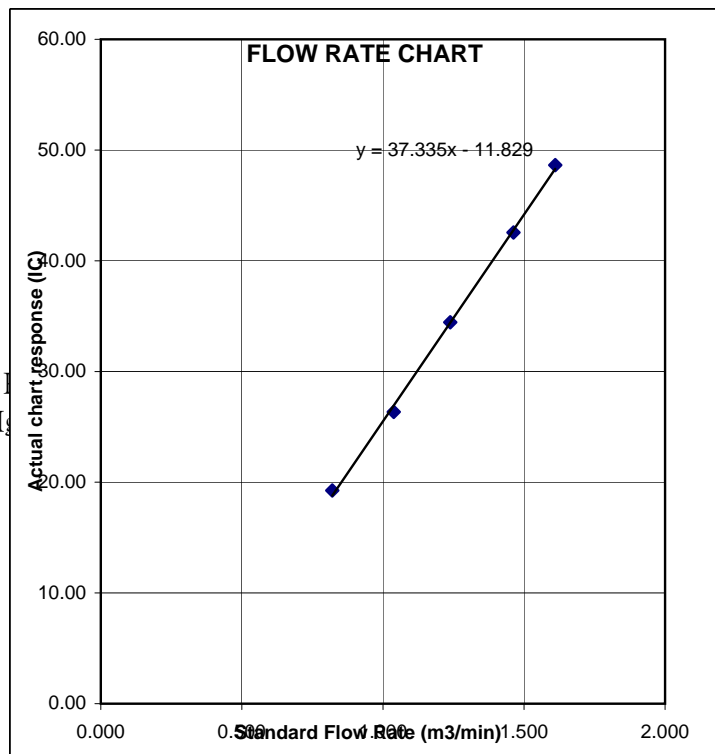

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Tai Hing Car Shop (Scattered House near Route 6) Date of Calibration: 1-Apr-10
 Location ID : AM 6 Next Calibration Date: 1-Jun-10
 Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa) 1013.6 Corrected Pressure (mm Hg) 760.2
 Temperature (°C) 23.0 Temperature (K) 296

CALIBRATION ORIFICE

Make-> TISCH Qstd Slope -> 2.01546
 Model-> 515N Qstd Intercept -> -0.02851
 Serial # -> 10394

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION Slope = 38.5038 Intercept = -14.7612 Corr. coeff. = 0.9974
18	5.3	5.3	10.6	1.635	49	49.34	
13	3.9	3.9	7.8	1.405	38	38.26	
10	2.9	2.9	5.8	1.213	31	31.21	
7	2.0	2.0	4.0	1.010	24	24.17	
5	1.2	1.2	2.4	0.785	16	16.11	

Calculations :


$Q_{std} = 1/m[\sqrt{(H_2O(P_a/P_{std})(T_{std}/T_a))}-b]$
 $IC = I[\sqrt{(P_a/P_{std})(T_{std}/T_a)}$

 Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$1/m((I)[\sqrt{(298/T_{av})(P_{av}/760)}]-b)$

 m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

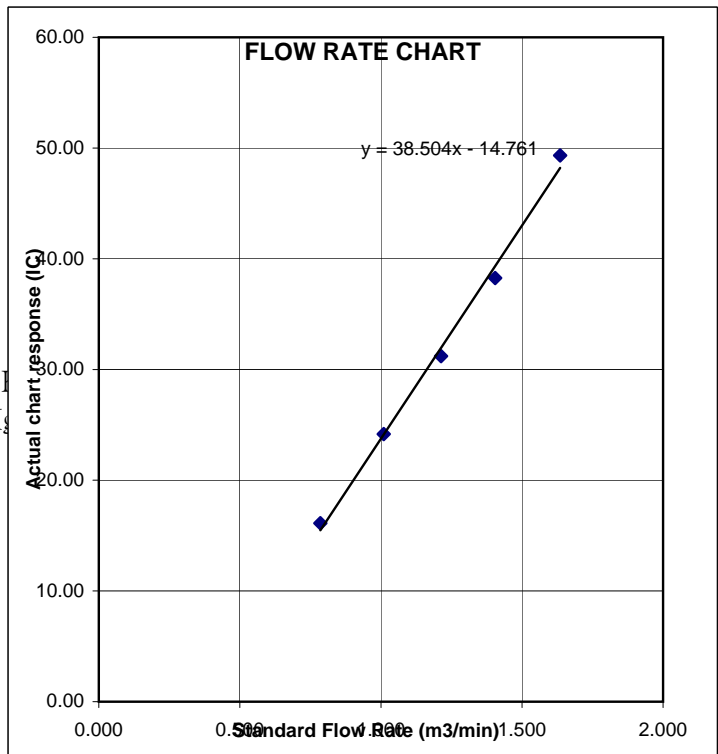

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Sha Po Pumping Station	Date of Calibration: 1-Apr-10
Location ID : AM5	Next Calibration Date: 1-Jun-10
	Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa)	1013.6	Corrected Pressure (mm Hg)	760.2
Temperature (°C)	23.0	Temperature (K)	296

CALIBRATION ORIFICE

Make-> TISCH	Qstd Slope -> 2.01546
Model-> 515N	Qstd Intercept -> -0.02851
Serial # -> 355	

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.2	5.2	10.4	1.620	48	48.33	Slope = 38.6975 Intercept = -15.4596 Corr. coeff. = 0.9966
13	4.3	4.3	8.6	1.474	41	41.28	
10	3.3	3.3	6.6	1.293	33	33.23	
7	2.3	2.3	4.6	1.082	26	26.18	
5	1.4	1.4	2.8	0.847	18	18.12	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H20(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

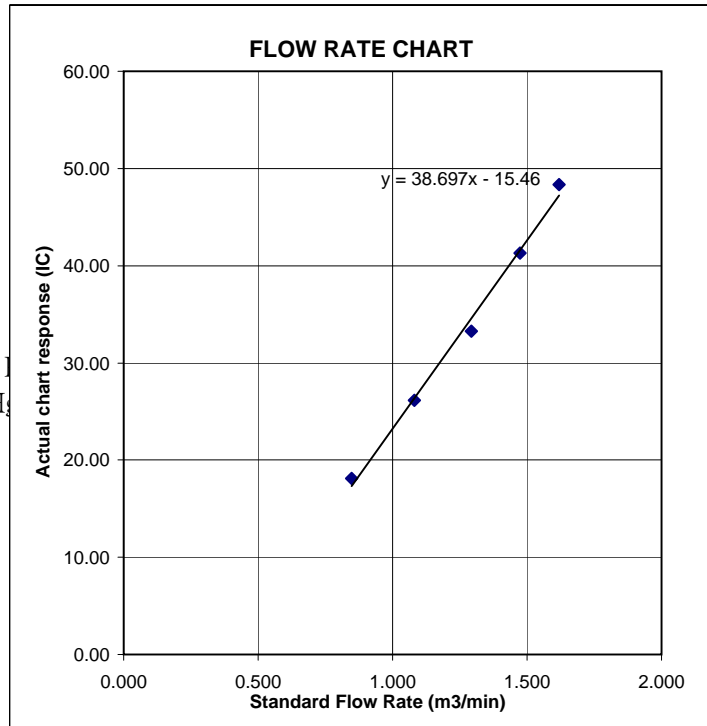

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : Nam Sang Wai	Date of Calibration: 26-Apr-10
Location ID : AM 1 (Designated)	Next Calibration Date: 26-Jun-10
Serial No: 0329	Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa)	1016.8	Corrected Pressure (mm Hg)	762.6
Temperature (°C)	21.6	Temperature (K)	295

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.01546
Model->	515N	Qstd Intercept ->	-0.02851
Serial # ->	0285		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.1	5.1	10.2	1.611	49	49.65	Slope = 41.9921 Intercept = ##### Corr. coeff. = 0.9979
13	4.2	4.2	8.4	1.463	41	41.54	
10	3.3	3.3	6.6	1.298	35	35.46	
7	2.4	2.4	4.8	1.109	28	28.37	
5	1.6	1.6	3.2	0.908	19	19.25	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$

$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate

IC = corrected chart responses

I = actual chart response

m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg]

Pstd = actual pressure during calibration (mm Hg

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$


m = sampler slope

b = sampler intercept

I = chart response

Tav = daily average temperature

Pav = daily average pressure

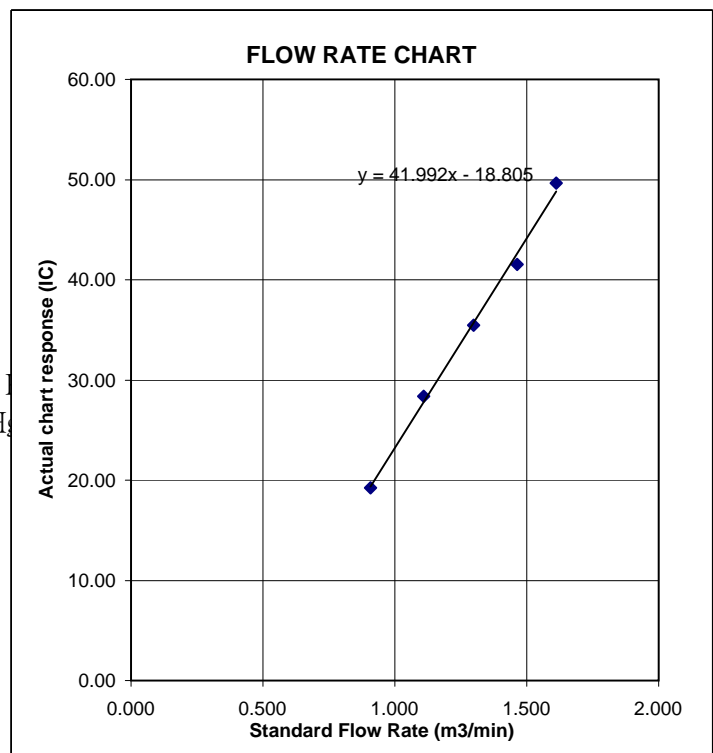

ANNEX I

METEOROLOGICAL DATA

Meteorological Data Extracted From the HK Observatory at Lau Fau Shan Weather Station


Date		Weather	Total Rain fall (mm)	Lau Fau Shan Weather Station			
				Mean Air Temp. (°C)	Wind Speed (km/h)	Mean Relative Humidity (%)	Wind Direction
1-Apr-10	Thu	Misty at first. Mainly fine in the afternoon. Light winds.	Trace	24.8	11.7	76	SE
2-Apr-10	Fri	Holiday					
3-Apr-10	Sat	Holiday					
4-Apr-10	Sun	Holiday					
5-Apr-10	Mon	Holiday					
6-Apr-10	Tue	Holiday					
7-Apr-10	Wed	Cloudy with rain at times. Misty. Fresh easterly winds, occasionally strong offshore	1.8	20.6	18	8.3	E
8-Apr-10	Thu	Cloudy with rain. A few squally thunderstorms at first.	9.6	16.6	13	83	E
9-Apr-10	Fri	Sunny periods. Light to moderate east to northeasterly winds.	Trace	19	6.7	81.7	E/NE
10-Apr-10	Sat	Cloudy with sunny intervals.	1.7	20.4	14	91.7	E/NE
11-Apr-10	Sun	Mainly cloudy with coastal fog.	Trace	24.7	20.7	84	S/SE
12-Apr-10	Mon	Cloudy with a few rain and fog patches.	0	26.8	12.2	79	S
13-Apr-10	Tue	Cloudy with a few rain patches.	0.9	25	17.5	81.5	S/SE
14-Apr-10	Wed	Cloudy with a few rain patches. Misty at first.	0.3	20.4	21.2	79	E
15-Apr-10	Thu	Cloudy with mist and a few rain patches.	8.2	15.4	16.5	90	E/NE
16-Apr-10	Fri	Cloudy with a few light rain patches.	Trace	15.1	10.7	78	E/NE
17-Apr-10	Sat	Misty. Sunny periods this afternoon.	2	19.1			
18-Apr-10	Sun	Cloudy with coastal fog. Sunny intervals.	3.1	20.7	10.5	84	E
19-Apr-10	Mon	Cloudy. Moderate east to southeasterly winds.	Trace	24.2	14	79	E/NE
20-Apr-10	Tue	Foggy. Mainly cloudy. A few rain patches at first.	1.1	25.2	20.5	81.5	S/SE
21-Apr-10	Wed	Sunny periods in the afternoon. A few showers tonight.	0	27.1	20.5	75.5	S/SE
22-Apr-10	Thu	Rainy with a few squally thunderstorms. Fresh northerly winds.	6.8	23.8	29.5	86	S/SE
23-Apr-10	Fri	Mainly fine and dry in the afternoon. Cloudy tonight.	0	21.9	21	66.5	N/NE
24-Apr-10	Sat	Sunny intervals during the day. Rain tonight.	Trace	22.7	15.2	57.5	E
25-Apr-10	Sun	Cloudy with a few rain patches.	0	22.7	13.5	64	E
26-Apr-10	Mon	Visibility relatively low.	0.2	22.3	14.5	79	E/NE
27-Apr-10	Tue	Mainly cloudy. Light to moderate northerly winds	Trace	21.2	11	75.7	N/NE
28-Apr-10	Wed	Mainly cloudy with one or two light rain patches.	Trace	22.5	9.5	82	W/SW
29-Apr-10	Thu	Cloudy with occasional rain.	40.6	21.7	13.5	84	E/NE
30-Apr-10	Fri	Cloudy with a few rain patches	0.6	21.4	13.2	78.5	E/NE

ANNEX J


**GRAPHICAL PLOTS OF AIR QUALITY AND CONSTRUCTION NOISE
MONITORING RESULTS**

AIR QUALITY

Air Quality Monitoring Results

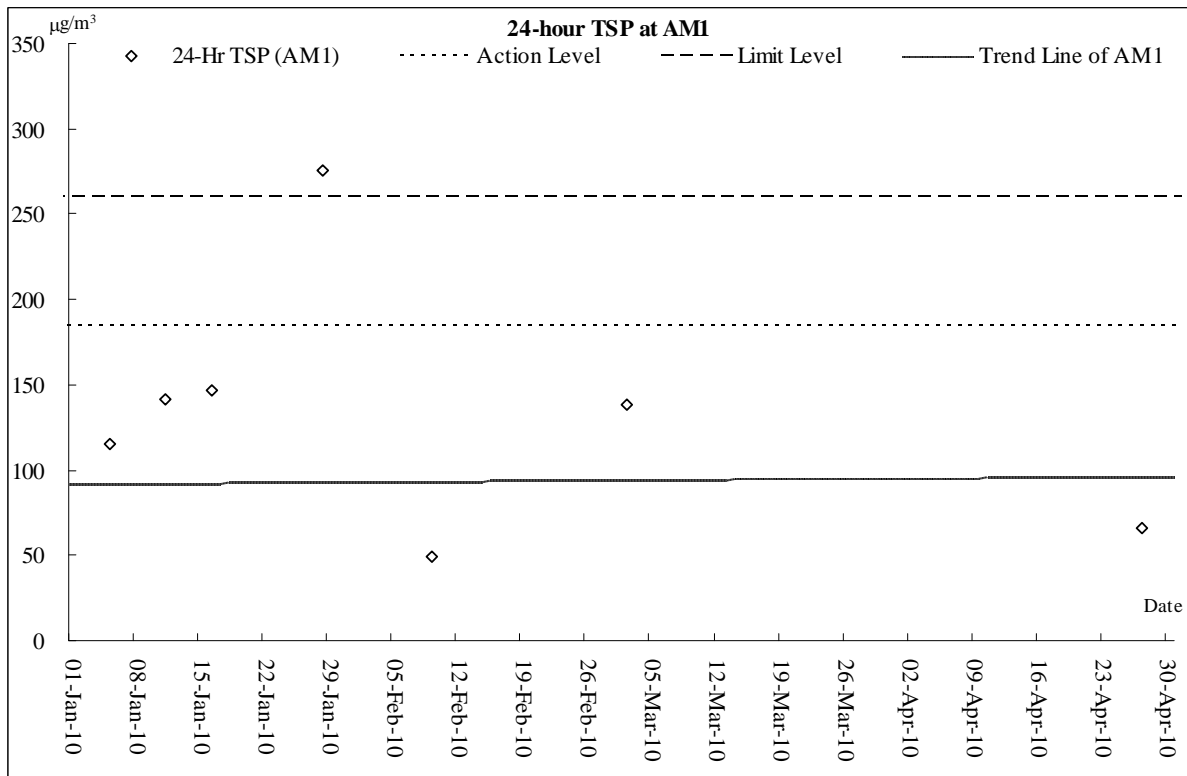


Note: power failure occurred on 22 January, 3, 18, 24 February, 8, 13, 19, 25 March, 9, 15 and 21 April 2010 therefore no result on plotting is shown.

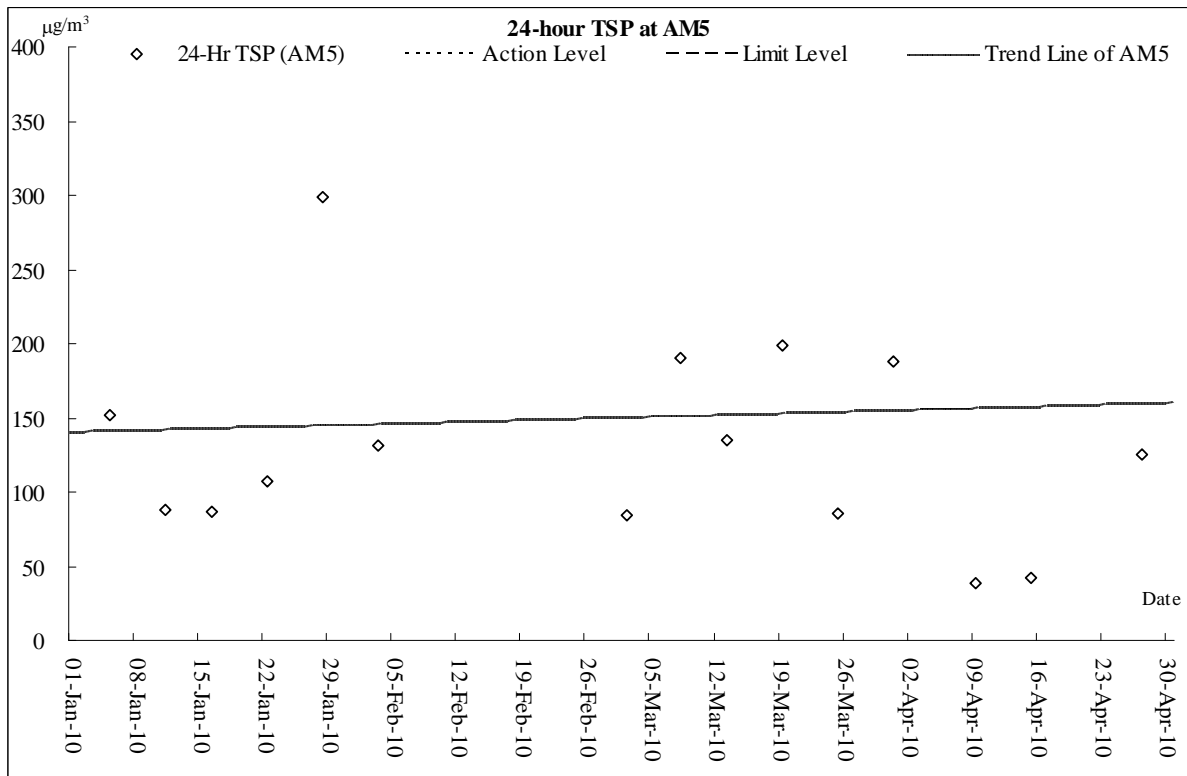


Note: cannot access the monitoring location between 4 and 24 February 2010 due to Lunar New Year holiday landowner's workshop closed and power failure occurred on 21 April 2010 therefore no result on plotting is shown.

Air Quality Monitoring Results

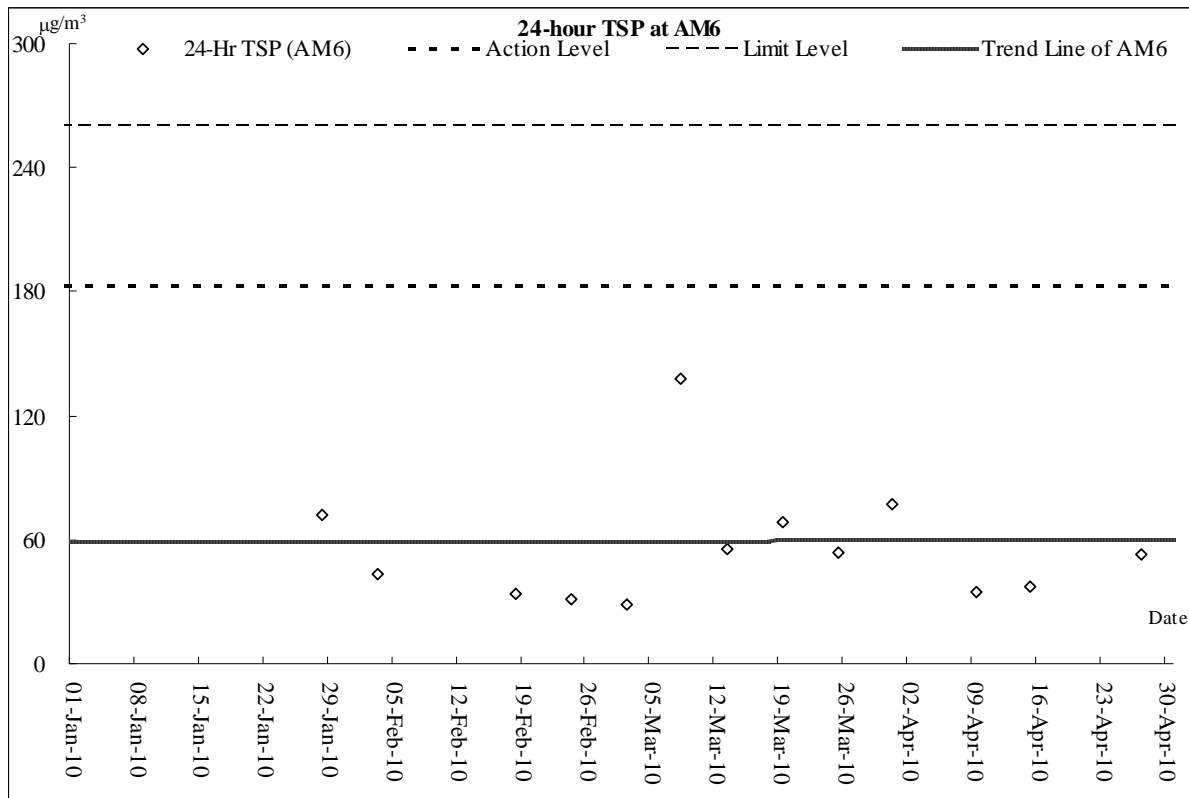



Note: power failure occurred on 29 December 2009 and 5, 11, 16, 22 January, 9 February and 21 April 2010 therefore no result on plotting is shown.

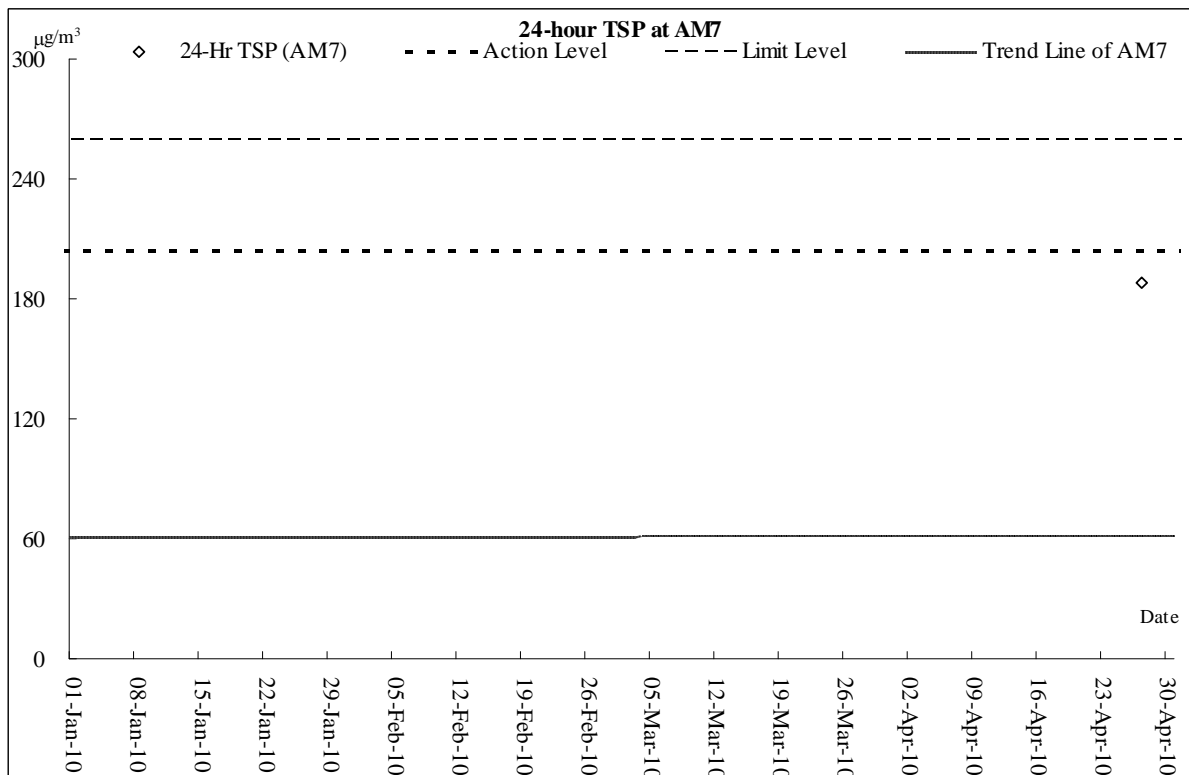



Note: power failure occurred between 16 November 2009 and 25 April 2010, therefore no result on plotting is shown.


CONSTRUCTION NOISE

Construction Noise Monitoring Results

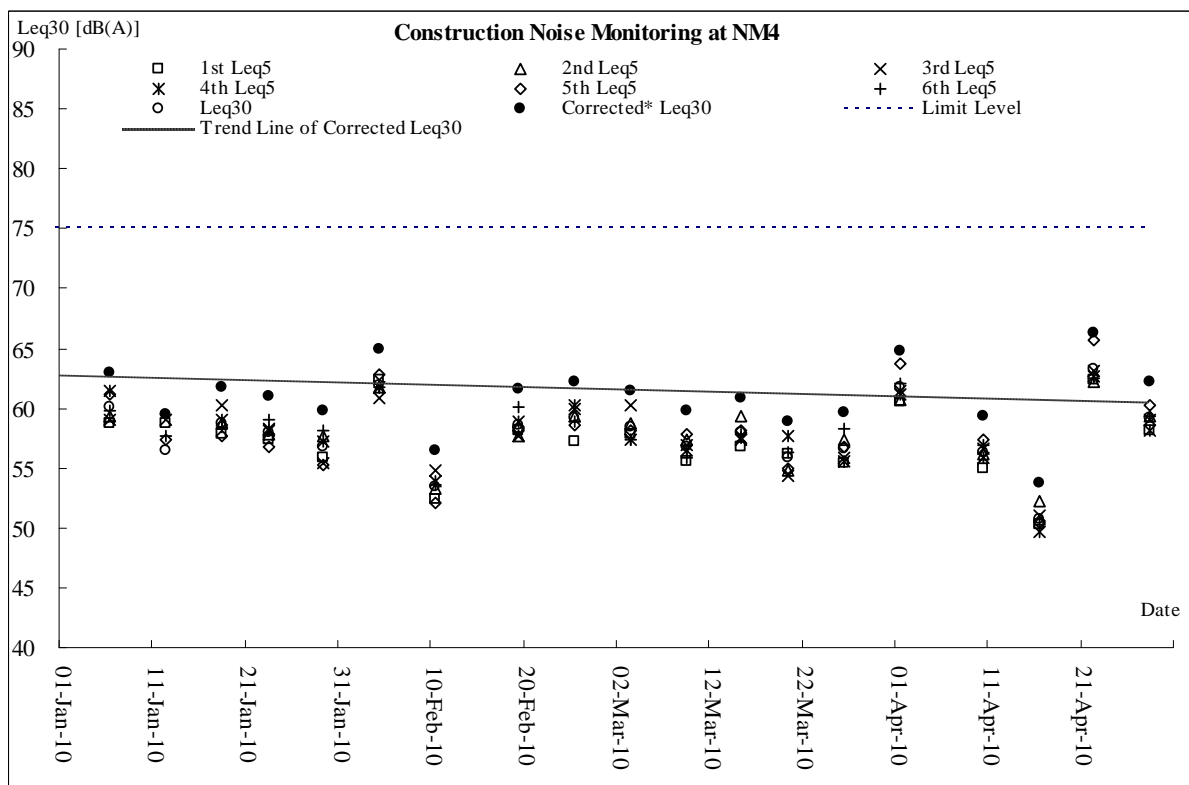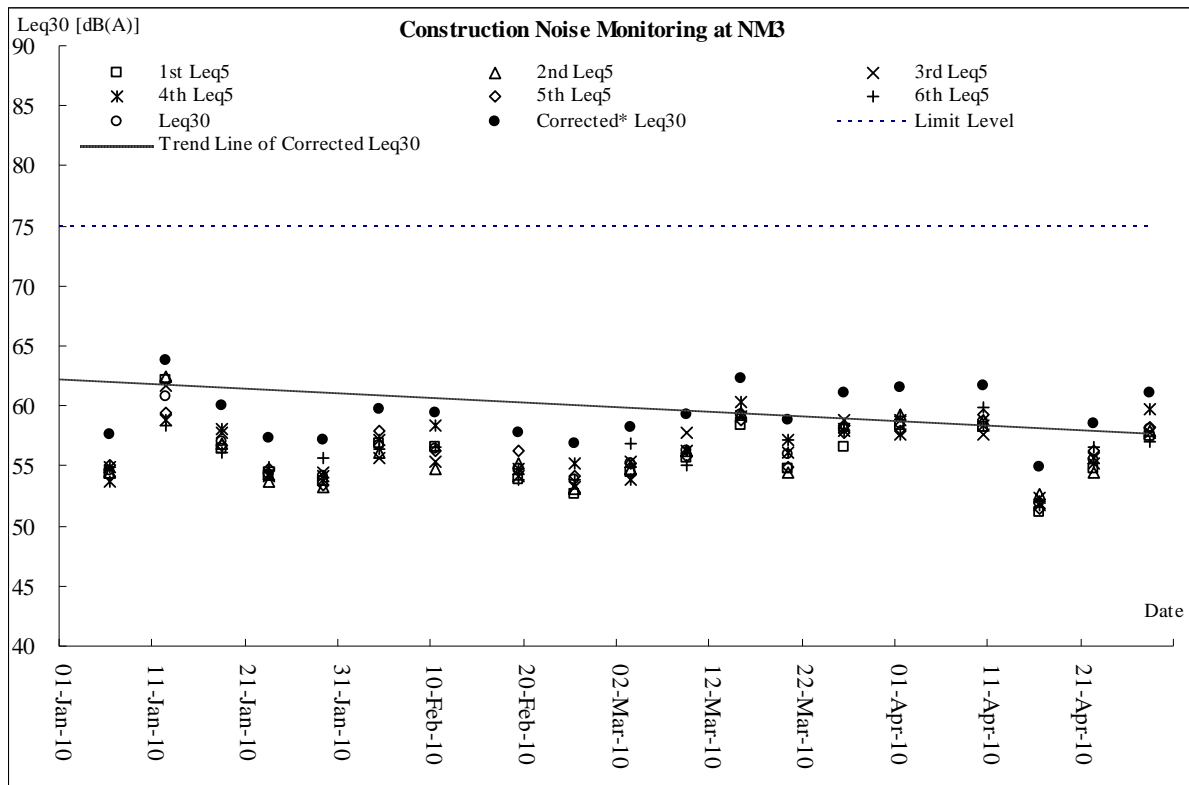

Construction Noise Monitoring Results

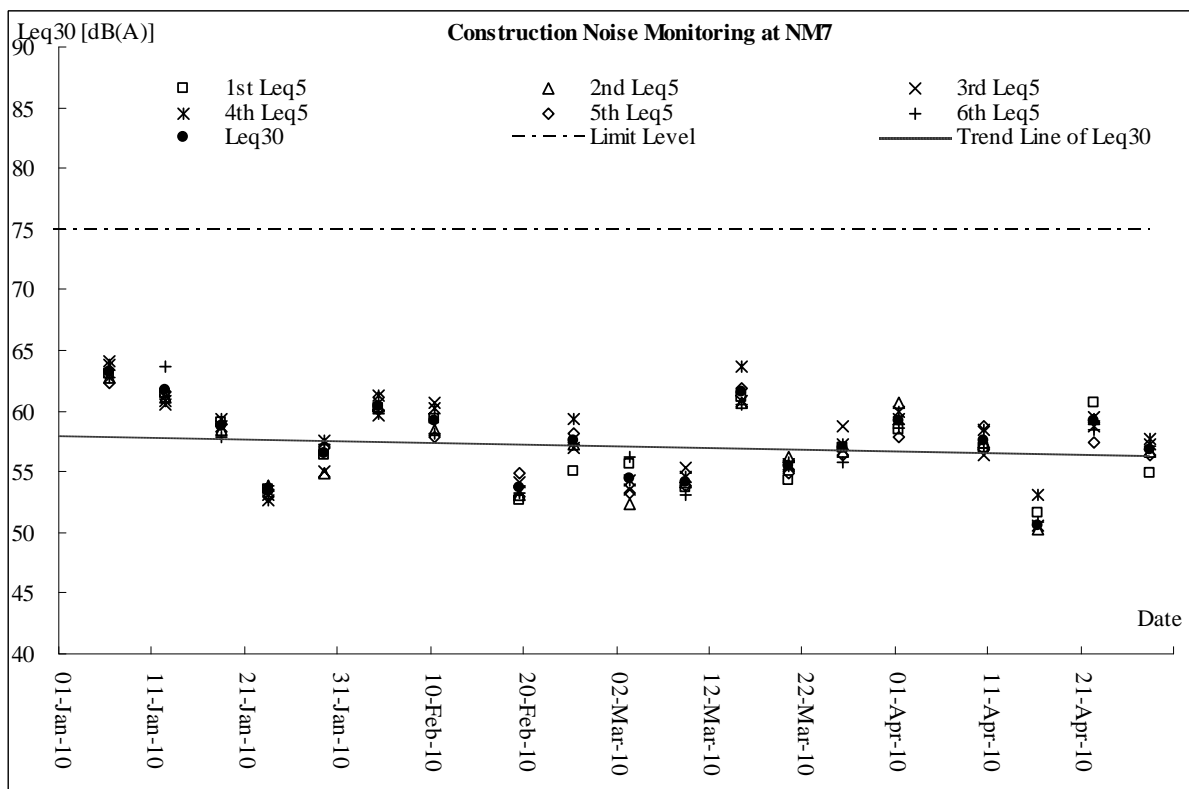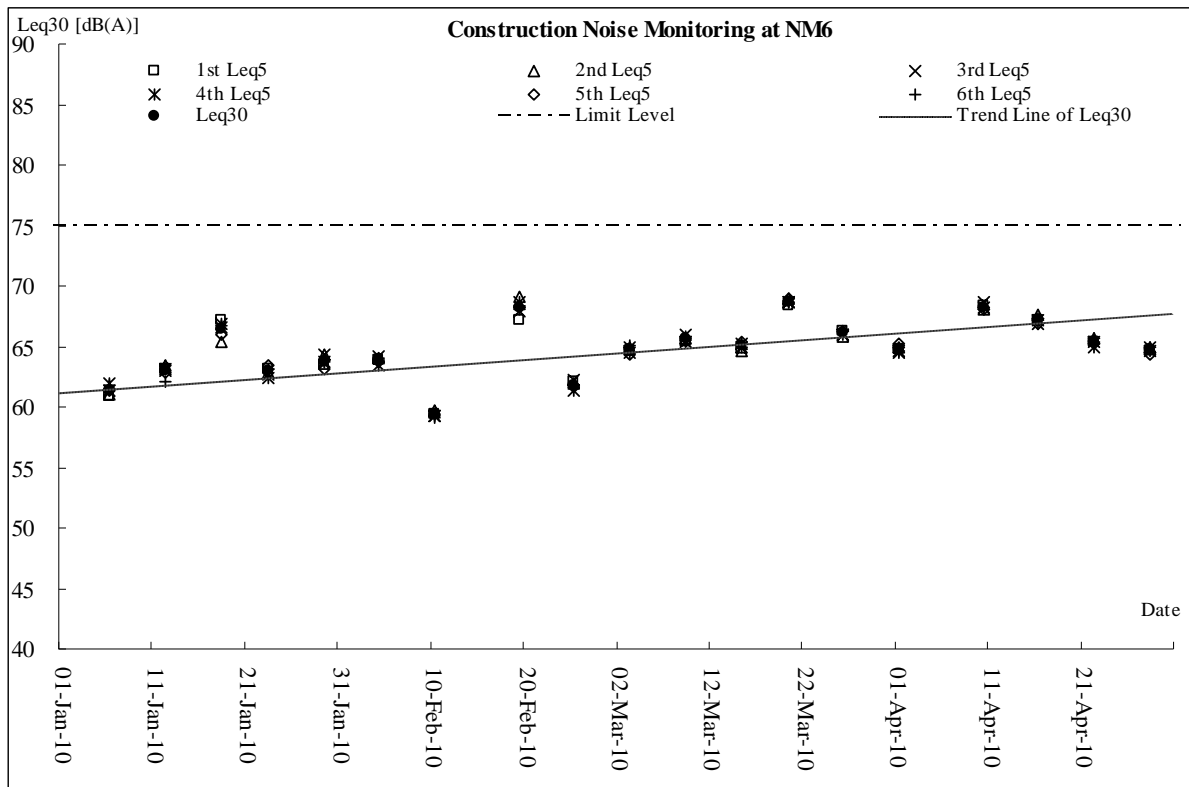



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C102286

Calibration Report

ITEM TESTED

DESCRIPTION : Integrating Sound Level Meter (EQ006)
MANUFACTURER : Bruel & Kjaer
MODEL NO. : 2238
SERIAL NO. : 2285762

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$ RELATIVE HUMIDITY : $(55 \pm 20)\%$
LINE VOLTAGE : ---

TEST SPECIFICATIONS

Calibration check

DATE OF TEST : 26 April 2010

JOB NO. : IC10-0951

TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested by :


W L Lai

Date : 27 April 2010

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Page 1 of 4

ANNEX K

PROFORMA OF SITE INSPECTION & IEC AUDIT

Project DC/2005/02 Construction of Sewers, Rising Mains & Sewage Pumping Station at Kam Tin, Nam Sang Wai and Au Tau in Yuen Long	Contractor: Leader Civil Engineering Corp. Ltd
Inspected by: ET Auditor: Ben Tam Contractor Rep: Edwin Leung IEC's Rep: RE's Rep: WK Tsang	Engineer: Babtie Asia Ltd IEC: Mott MacDonald Hong Kong Ltd Environmental Team: Action-United Environmental Services & Consulting Inspection Date & Time: 9 April 2010 (10:00am) Checklist Reference No.: DSD-AT090410

General Meteorological Information

Weather Sunny Fine Cloudy Overcast Drizzle Rain Hazy
Temp: °C
Humidity: High (RH > 90%) Moderate (90% > RH > 50%) Low (RH < 50%)
Wind: Calm Light Breeze Strong

Air Quality

	Yes	NO	NA	NC	Follow-up	Remarks
Is hoarding of not less than 2.4m provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are site vehicles traveling within controlled speed limit?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are site vehicles movement confined to designated haul roads?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are public roads outside site exits kept clean and free from dust?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are haul roads and unpaved surfaces watered regularly to avoid dust generation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there wheel washing facilities provided at site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is water spraying used during the main dust-generating activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are the excavated or stockpile of dusty materials kept wet or covered by impermeable/tarpaulin sheet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is exposed area of ground covered or watered frequently?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are load on vehicles covered by clean impervious sheeting?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are vehicles and equipment switched off while not in use?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are smoky emissions from plants/equipment avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is open burning avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Observable dust sources <input type="checkbox"/> Wind erosion	<input checked="" type="checkbox"/>	NA				
<input type="checkbox"/> Loading/unloading of materials	<input type="checkbox"/>	Others	_____			

Construction Noise

Are the construction works scheduled to minimize noise nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are the works or equipment sited to minimize noise nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are all plant and equipment well maintained and in good operating condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is powered mechanical equipment covered or shielded by appropriate acoustic materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is silenced equipment used where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are noise enclosures or noise barriers used where necessary?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Does specified equipment has valid noise label?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are Construction Noise Permits (CNPs) available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Major Noise Source <input type="checkbox"/> Traffic	<input checked="" type="checkbox"/>	Construction activities inside the site				
<input type="checkbox"/> Construction activities outside of site	<input type="checkbox"/>	Others	Nil _____			

Water Quality & Drainage		Yes	NO	NA	NC	Follow-up	Remarks
Is a wastewater discharge license obtained for the Project?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is site effluent discharged in accordance with the discharge license?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is the discharge of silty water avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is drainage adequate?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is drainage system well maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there temporary ditches for runoff discharge into appropriate watercourse?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there sedimentation tanks for settling runoff prior to discharge?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are the sedimentation tanks: Constructed of pre-formed individual cells?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
With adequate capacity?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Free from silt and sediment?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there neutralization tanks for concrete batching/mixing discharge?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there oil interceptors in drainage system?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is wheel wash facility provided at every site exit?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are vehicles and plant cleaned of earth, mud & debris before leaving the site?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are wheel washing facilities regularly inspected and maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are toilets provided on site? If so, are they properly maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are manholes covered and sealed?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is oil leakage or spillage avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Waste Management and Potential Land Contamination							
General Refuse:	Are receptacles (rubbish bins) available?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is there regular and proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is proper sorting and recycling implemented?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Construction Waste:	Is generation of construction waste minimized?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is waste sorting implemented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is construction waste reused where practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is construction waste properly disposed of?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are disposal records available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Chemical waste/waste oil	Is there designated storage area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is chemical waste stored properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is there proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is chemical waste license available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Excavated Materials	Do excavated materials appear uncontaminated?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are appropriate procedures followed if contaminated materials exist?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are disposal records available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Chemical/Fuel	Is chemical/fuel stored in bounded area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is bund capacity adequate (>110% of the largest tank)?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are storage areas lockable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is foam, oil, grease or other objectionable matters in water or nearby drains of sewer avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____

Remarks:

Follow up

Nil

Observations Recorded in this Site Inspection:

No environmental issue was observed during the site inspection.

Signatures:

Env. Auditor

Contractor's Representative

IC(E) Auditor

Witness by RE's Representative



Name :Ben Tam

Name: Edwin Leung

Name:

Name:

Project	DC/2005/02 Construction of Sewers, Rising Mains & Sewage Pumping Station at Kam Tin, Nam Sang Wai and Au Tau in Yuen Long	Contractor:	Leader Civil Engineering Corp. Ltd
Inspected by:	ET Auditor: Ben Tam	Engineer:	Babtie Asia Ltd
	Contractor Rep: Edwin Leung	IEC:	Mott MacDonald Hong Kong Ltd
	IEC's Rep:	Environmental Team:	Action-United Environmental Services & Consulting
	RE's Rep: WK Tsang	Inspection Date & Time:	14 April 2010 (10:00am)
		Checklist Reference No.:	DSD-AT140410

General Meteorological Information

Weather Sunny Fine Cloudy Overcast Drizzle Rain Hazy
Temp: °C
Humidity: High (RH > 90%) Moderate (90% > RH > 50%) Low (RH < 50%)
Wind: Calm Light Breeze Strong

Air Quality

	Yes	NO	NA	NC	Follow-up	Remarks
Is hoarding of not less than 2.4m provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are site vehicles traveling within controlled speed limit?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are site vehicles movement confined to designated haul roads?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are public roads outside site exits kept clean and free from dust?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Remark 1
Are haul roads and unpaved surfaces watered regularly to avoid dust generation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are there wheel washing facilities provided at site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is water spraying used during the main dust-generating activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are the excavated or stockpile of dusty materials kept wet or covered by impermeable/tarpaulin sheet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is exposed area of ground covered or watered frequently?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are load on vehicles covered by clean impervious sheeting?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are vehicles and equipment switched off while not in use?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are smoky emissions from plants/equipment avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is open burning avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Observable dust sources <input type="checkbox"/> Wind erosion	<input checked="" type="checkbox"/>	NA				
<input type="checkbox"/> Loading/unloading of materials	<input type="checkbox"/>	Others				

Construction Noise

Are the construction works scheduled to minimize noise nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are the works or equipment sited to minimize noise nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are all plant and equipment well maintained and in good operating condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is powered mechanical equipment covered or shielded by appropriate acoustic materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is silenced equipment used where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are noise enclosures or noise barriers used where necessary?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Does specified equipment has valid noise label?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are Construction Noise Permits (CNPs) available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Major Noise Source <input type="checkbox"/> Traffic	<input checked="" type="checkbox"/>	Construction activities inside the site				
<input type="checkbox"/> Construction activities outside of site	<input type="checkbox"/>	Others	Nil			

Water Quality & Drainage		Yes	NO	NA	NC	Follow-up	Remarks
Is a wastewater discharge license obtained for the Project?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is site effluent discharged in accordance with the discharge license?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is the discharge of silty water avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is drainage adequate?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is drainage system well maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there temporary ditches for runoff discharge into appropriate watercourse?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there sedimentation tanks for settling runoff prior to discharge?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are the sedimentation tanks: Constructed of pre-formed individual cells?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
With adequate capacity?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Free from silt and sediment?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there neutralization tanks for concrete batching/mixing discharge?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there oil interceptors in drainage system?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is wheel wash facility provided at every site exit?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are vehicles and plant cleaned of earth, mud & debris before leaving the site?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are wheel washing facilities regularly inspected and maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are toilets provided on site? If so, are they properly maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are manholes covered and sealed?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is oil leakage or spillage avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Waste Management and Potential Land Contamination							
General Refuse:	Are receptacles (rubbish bins) available?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is there regular and proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is proper sorting and recycling implemented?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Construction Waste:	Is generation of construction waste minimized?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is waste sorting implemented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is construction waste reused where practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is construction waste properly disposed of?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are disposal records available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Chemical waste/waste oil	Is there designated storage area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is chemical waste stored properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is there proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is chemical waste license available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Excavated Materials	Do excavated materials appear uncontaminated?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are appropriate procedures followed if contaminated materials exist?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are disposal records available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Chemical/Fuel	Is chemical/fuel stored in bounded area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is bund capacity adequate (>110% of the largest tank)?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are storage areas lockable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is foam, oil, grease or other objectionable matters in water or nearby drains of sewer avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____

Remarks:

Follow up

Nil

Observations Recorded in this Site Inspection:



Sand and mud tails was observed at the site exit, the contractor was reminded to keep the public roads outside site exits kept clean and free from dust.

Signatures:

Env. Auditor

Contractor's Representative

IC(E) Auditor

Witness by RE's Representative



Name :Ben Tam

Name: Edwin Leung

Name:

Name:

Project	DC/2005/02 Construction of Sewers, Rising Mains & Sewage Pumping Station at Kam Tin, Nam Sang Wai and Au Tau in Yuen Long	Contractor:	Leader Civil Engineering Corp. Ltd
Inspected by:	ET Auditor: Ben Tam	Engineer:	Babtie Asia Ltd
	Contractor Rep: Edwin Leung	IEC:	Mott MacDonald Hong Kong Ltd
	IEC's Rep:	Environmental Team:	Action-United Environmental Services & Consulting
	RE's Rep: WK Tsang	Inspection Date & Time:	20 April 2010 (10:00am)
		Checklist Reference No.:	DSD-AT200410

General Meteorological Information

Weather Sunny Fine Cloudy Overcast Drizzle Rain Hazy
Temp: °C
Humidity: High (RH > 90%) Moderate (90% > RH > 50%) Low (RH < 50%)
Wind: Calm Light Breeze Strong

Air Quality

	Yes	NO	NA	NC	Follow-up	Remarks
Is hoarding of not less than 2.4m provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are site vehicles traveling within controlled speed limit?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are site vehicles movement confined to designated haul roads?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are public roads outside site exits kept clean and free from dust?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are haul roads and unpaved surfaces watered regularly to avoid dust generation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are there wheel washing facilities provided at site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is water spraying used during the main dust-generating activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are the excavated or stockpile of dusty materials kept wet or covered by impermeable/tarpaulin sheet?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Remark 1
Is exposed area of ground covered or watered frequently?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are load on vehicles covered by clean impervious sheeting?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are vehicles and equipment switched off while not in use?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are smoky emissions from plants/equipment avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is open burning avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Observable dust sources <input type="checkbox"/> Wind erosion	<input checked="" type="checkbox"/>	NA				
<input type="checkbox"/> Loading/unloading of materials	<input type="checkbox"/>	Others				

Construction Noise

Are the construction works scheduled to minimize noise nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are the works or equipment sited to minimize noise nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are all plant and equipment well maintained and in good operating condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is powered mechanical equipment covered or shielded by appropriate acoustic materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Is silenced equipment used where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are noise enclosures or noise barriers used where necessary?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Does specified equipment has valid noise label?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Are Construction Noise Permits (CNPs) available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Major Noise Source <input type="checkbox"/> Traffic	<input checked="" type="checkbox"/>	Construction activities inside the site				
<input type="checkbox"/> Construction activities outside of site	<input type="checkbox"/>	Others	Nil			

Water Quality & Drainage		Yes	NO	NA	NC	Follow-up	Remarks
Is a wastewater discharge license obtained for the Project?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is site effluent discharged in accordance with the discharge license?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is the discharge of silty water avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is drainage adequate?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is drainage system well maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there temporary ditches for runoff discharge into appropriate watercourse?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there sedimentation tanks for settling runoff prior to discharge?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are the sedimentation tanks:	Constructed of pre-formed individual cells?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	With adequate capacity?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Free from silt and sediment?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there neutralization tanks for concrete batching/mixing discharge?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there oil interceptors in drainage system?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is wheel wash facility provided at every site exit?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are vehicles and plant cleaned of earth, mud & debris before leaving the site?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are wheel washing facilities regularly inspected and maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are toilets provided on site? If so, are they properly maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are manholes covered and sealed?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is oil leakage or spillage avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Waste Management and Potential Land Contamination							
General Refuse:	Are receptacles (rubbish bins) available?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is there regular and proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is proper sorting and recycling implemented?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Construction Waste:	Is generation of construction waste minimized?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is waste sorting implemented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is construction waste reused where practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is construction waste properly disposed of?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are disposal records available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Chemical waste/waste oil	Is there designated storage area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is chemical waste stored properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is there proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is chemical waste license available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Excavated Materials	Do excavated materials appear uncontaminated?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are appropriate procedures followed if contaminated materials exist?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are disposal records available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Chemical/Fuel	Is chemical/fuel stored in bounded area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is bund capacity adequate (>110% of the largest tank)?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are storage areas lockable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is foam, oil, grease or other objectionable matters in water or nearby drains of sewer avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____

Remarks:

Follow up

Sand and mud tails at the site exit was cleared.

Observations Recorded in this Site Inspection:



Stock pile without cover was observed at Nam San Wai Road, the contractor was reminded to provide mitigation measures to prevent dust generation.

Signatures:

Env. Auditor

Contractor's Representative

IC(E) Auditor

Witness by RE's Representative



Name :Ben Tam

Name: Edwin Leung

Name:

Name:

Project	DC/2005/02 Construction of Sewers, Rising Mains & Sewage Pumping Station at Kam Tin, Nam Sang Wai and Au Tau in Yuen Long	Contractor:	Leader Civil Engineering Corp. Ltd
		Engineer:	Babtie Asia Ltd
Inspected by:	ET Auditor: Ben Tam	IEC:	Mott MacDonald Hong Kong Ltd
	Contractor Rep: Edwin Leung	Environmental Team:	Action-United Environmental Services & Consulting
	IEC's Rep: Issac Chu	Inspection Date & Time:	27 April 2010 (10:00am)
	RE's Rep: WK Tsang	Checklist Reference No.:	DSD-AT270410

General Meteorological Information

Weather Sunny Fine Cloudy Overcast Drizzle Rain Hazy
Temp: °C
Humidity: High (RH > 90%) Moderate (90% > RH > 50%) Low (RH < 50%)
Wind: Calm Light Breeze Strong

Air Quality

	Yes	NO	NA	NC	Follow-up	Remarks
Is hoarding of not less than 2.4m provided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are site vehicles traveling within controlled speed limit?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are site vehicles movement confined to designated haul roads?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are public roads outside site exits kept clean and free from dust?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are haul roads and unpaved surfaces watered regularly to avoid dust generation?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there wheel washing facilities provided at site exits?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is water spraying used during the main dust-generating activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are the excavated or stockpile of dusty materials kept wet or covered by impermeable/tarpaulin sheet?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is exposed area of ground covered or watered frequently?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are load on vehicles covered by clean impervious sheeting?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are vehicles and equipment switched off while not in use?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are smoky emissions from plants/equipment avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is open burning avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Observable dust sources <input type="checkbox"/> Wind erosion	<input checked="" type="checkbox"/>	NA				
<input type="checkbox"/> Loading/unloading of materials	<input type="checkbox"/>	Others	_____			

Construction Noise

Are the construction works scheduled to minimize noise nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are the works or equipment sited to minimize noise nuisance?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are all plant and equipment well maintained and in good operating condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is powered mechanical equipment covered or shielded by appropriate acoustic materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is silenced equipment used where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are noise enclosures or noise barriers used where necessary?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Does specified equipment has valid noise label?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are Construction Noise Permits (CNPs) available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Major Noise Source <input type="checkbox"/> Traffic	<input checked="" type="checkbox"/>	Construction activities inside the site				
<input type="checkbox"/> Construction activities outside of site	<input type="checkbox"/>	Others	Nil _____			

Water Quality & Drainage		Yes	NO	NA	NC	Follow-up	Remarks
Is a wastewater discharge license obtained for the Project?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is site effluent discharged in accordance with the discharge license?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is the discharge of silty water avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is drainage adequate?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is drainage system well maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there temporary ditches for runoff discharge into appropriate watercourse?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there sedimentation tanks for settling runoff prior to discharge?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are the sedimentation tanks: Constructed of pre-formed individual cells?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
With adequate capacity?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Free from silt and sediment?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there neutralization tanks for concrete batching/mixing discharge?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are there oil interceptors in drainage system?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is wheel wash facility provided at every site exit?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are vehicles and plant cleaned of earth, mud & debris before leaving the site?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are wheel washing facilities regularly inspected and maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are toilets provided on site? If so, are they properly maintained?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Are manholes covered and sealed?		<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is oil leakage or spillage avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Waste Management and Potential Land Contamination							
General Refuse:	Are receptacles (rubbish bins) available?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is there regular and proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is proper sorting and recycling implemented?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Construction Waste:	Is generation of construction waste minimized?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is waste sorting implemented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is construction waste reused where practicable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is construction waste properly disposed of?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are disposal records available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Chemical waste/waste oil	Is there designated storage area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is chemical waste stored properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is there proper disposal?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is chemical waste license available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Excavated Materials	Do excavated materials appear uncontaminated?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are appropriate procedures followed if contaminated materials exist?	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are disposal records available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Chemical/Fuel	Is chemical/fuel stored in bounded area?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Is bund capacity adequate (>110% of the largest tank)?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
	Are storage areas lockable?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____
Is foam, oil, grease or other objectionable matters in water or nearby drains of sewer avoided?		<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	_____

Remarks:

Follow up

Stockpile at Nam San Wai Road was removed.

Observations Recorded in this Site Inspection:

No environmental issue was observed during the site inspection.

Signatures:

Env. Auditor

Contractor's Representative

IC(E) Auditor

Witness by RE's Representative



Name :Ben Tam

Name: Edwin Leung

Name:

Name:
