



PROJECT No.: TCS/00512/09

**DSD CONTRACT NO. DC/2009/13
CONSTRUCTION OF SEWAGE TREATMENT WORKS AT
YUNG SHUE WAN AND SOK KWU WAN**

**YUNG SHUE WAN PORTION AREA
MONTHLY ENVIRONMENTAL MONITORING AND AUDIT
(EM&A) REPORT (No.13) – SEPTEMBER 2011**

PREPARED FOR
LEADER CIVIL ENGINEERING CORPORATION LIMITED

Quality Index

Date	Reference No.	Prepared By	Approved By
14 October 2011	TCS00512/09/600/R0346v2		
		Nicola Hon Environmental Consultant	T.W. Tam Environmental Team Leader

Version	Date	Description
1	7 October 2011	First Submission
2	14 October 2011	Amended against IEC's comments on 10 October 2011

Scott Wilson CDM Joint Venture

Chief Engineer/Harbour Area Treatment Scheme
Drainage Services Department
5/F Western Magistracy
2A Pok Fu Lam Road
Hong Kong

Your reference:

Our reference: 05117/6/16/382143

Date: 17 October 2011

Attention: Mr. C K Au


BY FAX AND EMAIL

Dear Sirs,

Contract No. DC/2009/13
Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan
Yung Shue Wan Portion Area
Monthly Environmental Monitoring and Audit (EM&A) Report No. 13 (September 2011)

We refer to the Monthly EM&A Monitoring Report No. 13 for September 2011 received under cover of the email from the Environmental Team, Action-United Environmental Services and Consulting (AUES), dated on 14 October 2011. We have no comment and have verified the captioned report.

Yours faithfully
SCOTT WILSON CDM JOINT VENTURE



Rodney Ip

ICWR/SYSL/ecwc

cc Leader Civil Engineering (Attn: Mr Vincent Chan)
 AUES (Attn: Mr T.W. Tam)
 ER/LAMMA (Attn: Mr Neil Wong)
 CDM (Attn: Mr Mark Sin)

EXECUTIVE SUMMARY

ES.01. This is the 13th monthly Environmental Monitoring and Audit (EM&A) for Yung Shue Wan (hereinafter ‘this Report’) for the designated works under Environmental Permit [EP-282/2007], covering a period from 1 to 30 September 2011 (hereinafter ‘the Reporting Period’).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES.02. Environmental monitoring activities under the EM&A programme in this Reporting Period are summarized in the following table.

Issues	Environmental Monitoring Parameters / Inspection	Occasions
Air Quality	1-hour TSP	30
	24-hour TSP	10
Construction Noise	Leq (30min) Daytime	5
Water Quality	Marine Water Sampling	14
Ecology	Coral Monitoring	4
Inspection / Audit	ET Regular Environmental Site Inspection	4

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES.03. No exceedance in construction noise, air quality and water quality monitoring were recorded in this Reporting Period. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental Issues	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	0	0	0	--	--
	24-hour TSP	0	0	0	--	--
Construction Noise	Leq _{30min} Daytime	0	0	0	--	--
Water Quality	DO	0	0	0	--	--
	Turbidity	0	0	0	--	--
	SS	0	0	0	--	--
Ecology (Coral)	Sediment Cover (%)	0	0	0	--	--
	Bleaching (%)	0	0	0	--	--
	Mortality (%)	0	0	0	--	--

Note: NOE – Notification of Exceedance

ENVIRONMENTAL COMPLAINT

ES.04. No written or verbal complaint was recorded in this Reporting Period. The statistics of environmental complaint are summarized in the following table.

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
14 September 2010 – 31 August 2011	0	0	NA
1 – 30 September 2011	0	0	NA

NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES.05. No environmental summons or successful prosecutions were recorded in this Reporting Period. The statistics of environmental complaint are summarized in the following tables.

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Complaint Nature
14 September 2010 – 31 August 2011	0	0	NA
1 – 30 September 2011	0	0	NA

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Complaint Nature
14 September 2010 – 31 August 2011	0	0	NA
1 – 30 September 2011	0	0	NA

REPORTING CHANGE

ES.06. There are no reporting changes in this Reporting Period.

SITE INSPECTION BY EXTERNAL PARTIES

ES.07. No site inspection was undertaken by external parties i.e. Environmental Protection Department (EPD) or Agriculture, Fisheries and Conservation Department (AFCD) within the Reporting Period.

FUTURE KEY ISSUES

ES.08. During dry and windy season, construction dust would be the key environmental issue to concern. The construction dust mitigation measures identified at the EM&A Manual such as watering at haul road and covering of dusty material should be implemented and properly maintained.

ES.09. Nevertheless, the Contractor shall keep paying attention on the potential water impact as the construction site is adjacent to the coastline. Muddy water and other water quality pollutants via site surface water runoff into the sea body within Fish culture zone at Picnic Bay and the Secondary recreation contact subzone at Mo Tat Wan should be avoided. Therefore, mitigation measures for water quality should be fully implemented also.

TABLE OF CONTENTS

1	INTRODUCTION	1
	PROJECT BACKGROUND	1
	REPORT STRUCTURE	1
2	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	3
	PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE	3
	CONSTRUCTION PROGRESS	3
	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	3
3	SUMMARY OF BASELINE MONITORING REQUIREMENTS	4
	ENVIRONMENTAL ASPECT	4
	MONITORING LOCATIONS	4
	MONITORING FREQUENCY AND PERIOD	5
	MONITORING EQUIPMENT	6
	EQUIPMENT CALIBRATION	7
	METEOROLOGICAL INFORMATION	8
	DATA MANAGEMENT AND DATA QA/QC CONTROL	8
	DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	8
4	IMPACT MONITORING RESULTS - AIR QUALITY	10
5	IMPACT MONITORING RESULTS – CONSTRUCTION NOISE	11
6	IMPACT MONITORING RESULTS – WATER QUALITY	12
7	IMPACT MONITORING RESULTS – ECOLOGY MONITORING	14
8	WASTE MANAGEMENT	15
9	SITE INSPECTION	16
10	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	17
11	IMPLEMENTATION STATUS OF MITIGATION MEASURES	18
12	IMPACT FORECAST	24
13	CONCLUSIONS AND RECOMMENDATIONS	25
	CONCLUSIONS	25
	RECOMMENDATIONS	25

LIST OF TABLES

Table 2-1	Status of Environmental Licenses and Permits
Table 2-2	Status of EM&A Programme Submission
Table 3-1	Summary of EM&A Requirements
Table 3-2	Location of Air Quality Monitoring Station
Table 3-3	Location of Construction Noise Monitoring Station
Table 3-4	Location of Marine Water Quality Monitoring Station
Table 3-5	Action and Limit Levels for Air Quality
Table 3-6	Action and Limit Levels for Construction Noise
Table 3-7	Action and Limit Levels for Marine Water Quality
Table 3-8	Action and Limit Levels for Coral Monitoring
Table 4-1	Summary of 24-hour and 1-hour TSP Monitoring Results at AC02b
Table 4-2	Summary of 24-hour and 1-hour TSP Monitoring Results at AC04c
Table 5-1	Summarized of Construction Noise Monitoring Results at NC05
Table 6-1	Summary of Water Quality Results – Mid-ebb Tides (Dissolved Oxygen)
Table 6-2	Summary of Water Quality Results – Mid-ebb Tides (Turbidity & Suspended Solids)
Table 6-3	Summary of Water Quality Results – Mid-flood Tides (Dissolved Oxygen)
Table 6-4	Summary of Water Quality Results – Mid-flood Tides (Turbidity & Suspended Solids)
Table 6-5	Summarized Exceedances of Marine Water Quality
Table 8-1	Summary of Quantities of Inert C&D Materials
Table 8-2	Summary of Quantities of C&D Wastes
Table 9-1	Site Observations
Table 10-1	Statistical Summary of Environmental Complaints
Table 10-2	Statistical Summary of Environmental Summons
Table 10-3	Statistical Summary of Environmental Prosecution
Table 11-1	Environmental Mitigation Measures

LIST OF APPENDICES

Appendix A	Site Layout Plan – Yung Shue Wan Portion Area
Appendix B	Organization Structure and Contact Details of Relevant Parties
Appendix C	A Master and Three Months Rolling Construction Programme
Appendix D	Location of Monitoring Stations (Air Quality / Construction Noise / Water Quality/ Dive Surveys of Coral)
Appendix E	Monitoring Equipments Calibration Certificate
Appendix F	Event and Action Plan
Appendix G	Monitoring Data Sheet
Appendix H	Graphical Plots of Monitoring Results
Appendix I	Meteorological Information
Appendix J	Monthly Summary Waste Flow Table
Appendix K	Weekly Site Inspection Checklist
Appendix L	Implementation Schedule of Mitigation Measures
Appendix M	Impact Coral Monitoring Report

1 INTRODUCTION

PROJECT BACKGROUND

- 1.01 The Leader Civil Engineering Corporation Limited (Leader) has been awarded the *Contract DC/2009/13 - Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan* (the Project) by the Drainage Services Department (DSD) on 4 May 2010. The Project is part of an overall plan approved under a statutory EIA for Outlying Islands Sewerage Stage 1 Phase 2 Package J – Sok Kwu Wan Sewage Collection and Treatment (Register No. AEIAR-075/2003) and Disposal Facilities and Outlying Islands Sewerage Stage 1 Phase 1 Package C – Yung Shue Wan Sewage Treatment Works and Outfall (Register No. EIA-124/BC). The Environmental Permit (EP) No. EP-281/2007 and EP-282/2007 for the Project have been obtained by the DSD on 29 June 2007 for the relevant works. After July 2009, EP-281/2007/A instead EP-281/2007 is EP for Sok Kwu Wan relevant Works.
- 1.02 The Project involves construction of sewage treatment works at Sok Kwu Wan and Yung Shue Wan with a capacity of 1,430m³/day and 2,850m³/day respectively to provide secondary treatment, construction of 2 pumping stations at Sok Kwu Wan and 1 pumping station at Yung Shue Wan, construction of submarine outfall from the coastline and laying of underground sewerage pipeline. The site layout plan for the captioned work under the Project is showing in **Appendix A**
- 1.03 According to the Particular Specification (PS) and **Appendix 25** of the Project, Leader should establish an Environmental Team (ET) to implement the environmental monitoring and auditing works to fulfill the requirements as stipulated in the EM&A Manual. This EM&A Manual is referred to the Appendix D of the Review Report on EIA Study – Yung Shue Wan (Final) in January 2007 (Agreement No. CE 20/2005(DS)).
- 1.04 Action-United Environmental Services and Consulting (AUES) has been commissioned by Leader as the ET to implement the relevant EM&A programme. Organization chart of the Environmental Team for the Project is shown in **Appendix B**. For ease of reporting, the proposed EM&A programme for baseline and impact monitoring is split to following two stand-alone parts:
- (a) Proposed EM&A Programme for Baseline and Impact Monitoring – Sok Kwu Wan (under EP No. 281/2007/A varied on 23 September 2009)
 - (b) Proposed EM&A Programme for Baseline and Impact Monitoring – Yung Shue Wan (under EP No. 282/2007)
- 1.05 According to the EM&A Manuals of Sok Kwu Wan and Yung Shue Wan, baseline water quality monitoring should be carried out for consecutive six months before the marine work commencement. Therefore, the baseline reports of Sok Kwu Wan and Yung Shue Wan are divided to two volumes i.e. the Volume 1 for air quality and noise monitoring; and the Volume II for water quality monitoring for separate submission.
- 1.06 This is the **13th** monthly EM&A Report for Yung Shue Wan Portion Area which presenting the monitoring results and inspection findings in the Reporting Period from **1 to 30 September 2011**.

REPORT STRUCTURE

- 1.07 The Monthly Environmental Monitoring and Audit (EM&A) Report – Yung Shue Wan is structured into the following sections:-

SECTION 1	INTRODUCTION
SECTION 2	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS
SECTION 3	SUMMARY OF MONITORING REQUIREMENTS
SECTION 4	AIR QUALITY MONITORING RESULTS
SECTION 5	CONSTRUCTION NOISE MONITORING RESULTS
SECTION 6	WATER QUALITY MONITORING RESULTS
SECTION 7	ECOLOGY MONITORING RESULTS
SECTION 8	WASTE MANAGEMENT
SECTION 9	SITE INSPECTIONS
SECTION 10	ENVIRONMENTAL COMPLAINTS AND NON-COMPLIANCE

SECTION 11	IMPLEMENTATION STATUES OF MITIGATION MEASURES
SECTION 12	IMPACT FORECAST
SECTION 13	CONCLUSIONS AND RECOMMENDATION

2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE

- 2.01 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in [Appendix B](#).

CONSTRUCTION PROGRESS

- 2.02 The master and three month rolling construction programme are enclosed in [Appendix C](#) and the major construction activities undertaken in this Reporting Period are listed below:-
- Construction of Control Room & Offices
 - Grit chambers
 - Grease separators
 - Subsoil drain
 - Slope stabilization works
 - Horizontal directional drilling (HDD) works

SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.03 Summary of the relevant permits, licences, and/or notifications on environmental protection for this Project in this Reporting Period is presented in [Table 2-1](#).

Table 2-1 Status of Environmental Licenses and Permits

Item	Description	License/Permit Status
1	Air Pollution Control (Construction Dust) Regulation	Notified 19/5/2010 Case No: 317486
2	Chemical Waste Producer Registration	Issued on 8/6/2010 WPN 5213-912-L2720-01
3	Water Pollution Control Ordinance	Issued on 22/9/2010 WT00007566-2010
4	Billing Account for Disposal of Construction Waste	Issued on 26 May 2010 A/C No: 7010815
5	Construction Noise Permit (no. GW-RS0624-11)	Issued on 8 July 2011 Valid from 8 July 2011 until 24 December 2011

- 2.04 Summary of the report submission for EM&A Programme is presented in [Table 2-2](#).

Table 2-2 Status of EM&A Programme Submission

Item	EM&A Programme Submission	Status
1	Proposed EM&A Programme for Baseline / Impact Monitoring – Yung Shue Wan (TCS00512/09/600/R0011 Ver.5)	Verified by IEC and submitted to EPD on 8 July 2010
2	Method Statement for Coral Monitoring – Yung Shue Wan (TCS00512/09/600/R0071 Ver.3)	Verified by IEC and submitted to EPD on 25 November 2010
3	Baseline Air and Noise Monitoring Report - Volume 1 (TCS00512/09/600/R0061 Ver.3)	Verified by IEC and submitted to EPD on 31 August 2010
4	Baseline Monitoring Report Volume 2 - Water Quality (TCS00512/09/600/R0158 Ver.2)	Verified by IEC and submitted to EPD on 10 March 2011
5	Baseline Survey for Coral Monitoring – Yung Shue Wan (TCS00512/09/600/R0132 Ver.3)	Verified by IEC and submitted to EPD on 17 February 2011
6	Methodology of Coral Tagging for Impact Monitoring – Yung Shue Wan	Verified by IEC and submitted to EPD on 28 March 2011
7	Coral Tagging Report (TCS00512/09/600/R0214 Ver.4)	Verified by IEC and submitted to EPD on 3 August 2011

3 SUMMARY OF BASELINE MONITORING REQUIREMENTS

ENVIRONMENTAL ASPECT

- 3.01 The EM&A baseline monitoring programme cover the following environmental issues:
- Air quality;
 - Construction noise;
 - Marine water quality; and
 - Ecology monitoring
- 3.02 The ET implements the EM&A programme in accordance with the aforementioned requirements. Detailed air quality, construction noise, water quality and ecology of the EM&A programme are presented in the following sub-sections.
- 3.03 A summary of the air, noise, marine water and ecology monitoring parameters is presented in *Table 3-1*:

Table 3-1 Summary of the EM&A Requirements

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> • 1-hour TSP Monitoring by Real-Time Portable Dust Meter; and • 24-hour TSP Monitoring by High Volume Air Sampler.
Noise	<ul style="list-style-type: none"> • Leq (30min) during normal working hours; and • Leq (15min) during Restricted Hours.
Marine Water Quality	<p><i>In-situ Measurements</i></p> <ul style="list-style-type: none"> • Dissolved Oxygen Concentration (DO) (mg/L); • Dissolved Oxygen Saturation (%); • Turbidity (NTU); • pH unit; • Salinity (ppt); • Water depth (m); and • Temperature (°C). <p><i>Laboratory Analysis</i></p> <ul style="list-style-type: none"> • Suspended Solids (SS) (mg/L)
Ecology	<ul style="list-style-type: none"> • Coral Monitoring

MONITORING LOCATIONS

Air Quality

- 3.04 Two designated monitoring stations, AC02a located at Yung Shue Wan Refuse Transfer Station and AC04 located at residential area nearby Yung Shue Wan football pitch, were recommended in the *EM&A Manual Section 2.5*. In order to identify and seek for the access of the air monitoring locations designated in the EM&A Manual, site visit was conducted by Leader and ET.
- 3.05 At the site visit, all designated monitoring locations were identified however the premises for high volume sampler installation were objected by the owner or the residents of nearby. So, alternative air monitoring locations were proposed in accordance with the criteria set out in *EM&A manual Section 2.5.2 and 2.5.3*. The proposed alternative air monitoring stations were accepted by the Engineer Representative (ER) and Independent Environmental Checker (IEC) and EPD for endorsement. Details of renewed air monitoring stations are described in *Table 3-2*. The graphical of air monitoring stations is shown in *Appendix D*.

Table 3-2 Location of Air Quality Monitoring Station

Sensitive Receiver	Location
AC02b	The entrance of RE's site office
AC04c	Next to a power transformer station TP208 Yung Shue Wan and adjacent to the road direct to the construction site

Construction Noise

- 3.06 According to *EM&A Manual Section 3.4*, one noise sensitive receivers (NC05) designated for the construction noise monitoring was recommended at Yung Shue Wan Portion Area of the Project. The designated monitoring station is identified and successfully granted the premises. The detailed construction noise monitoring station is described in **Table 3-3** and graphical is shown in **Appendix D**.

Table 3-3 Location of Construction Noise Monitoring Station

Sensitive Receiver	Location
NC05	Roof of North Lamma Clinic

Marine Water Quality

- 3.07 Two control stations (CY1 and CY2) and three impact stations (WY1-WY3) were recommended in the *EM&A Manual Section 4.5*. Impact stations WY1-WY3 were identified close to the sensitive receivers (the coral colonies in the vicinity of Yung Shue Wan, and secondary contact recreation subzone). It is proposed to monitor the impacts from the construction of the submarine outfall as well as the effluent discharge from the proposed STW on water quality. Two control stations: CY1 and CY2 were recommended at locations representative of the project site in its undisturbed condition and located at upstream and downstream of the works area. The marine water quality monitoring stations to be performed under the Project is described in **Table 3-4** and shown in **Appendix D**.

Table 3-4 Location of Marine Water Quality Monitoring Station

Station	Description	Coordinates	
		Easting	Northing
WY1	Coral colonies on seawall at STW site	829 170	809 550
WY2	Coral colonies at Shek kok Tsui	829 000	810 400
WY3	Coral colonies at O Tsai (headland N at SW ferry pier)	829 200	809 850
CY1 (flood)	Control Station	828 400	810 800
CY2 (ebb)	Control Station	828 000	808 800

Coral Monitoring

- 3.08 The coral monitoring stations to be performed under the Project is show in **Appendix D**. The details of the monitoring location could be referred to **Impact Coral Monitoring Report** which enclosed in **Appendix M**.

MONITORING FREQUENCY AND PERIOD

- 3.09 The Impact monitoring carried out in the EM&A programme is basically in accordance with the requirements in *EM&A Manual Sections 2.7, 3.6, 4.7, 4.8, 7.3 and 7.4*. The monitoring requirements are listed as follows:

Air Quality Monitoring

Parameters: 1-hour TSP and 24-hour TSP

Frequency: Once in every six days for 24-hour TSP and three times in every six days for 1-hour TSP

Duration: Throughout the construction period

Noise Monitoring

Parameters: $L_{eq(30min)}$ & $L_{eq(5min)}$, L_{10} and L_{90} .

$L_{eq(15min)}$ & $L_{eq(5min)}$, L_{10} and L_{90} during the construction undertaken during Restricted hours (19:00 to 07:00 hours next of normal working day and full day of public holiday and Sunday)

Frequency: Once per week during 0700-1900 hours on normal weekdays. Restricted hour monitoring should depend on conditions stipulated in Construction Noise Permit

Duration: Throughout the construction period

Marine Water Quality Monitoring

Parameters: Duplicate in-situ measurements: water depth, temperature, dissolved oxygen, pH, turbidity and salinity

HOKLAS-accredited laboratory analysis: suspended solids

Frequency: Three days a week, at mid ebb and mid flood tides. The interval between 2 sets of monitoring will be more than 36 hours

Sampling Depth (i.) Three depths: 1m below water surface, 1m above sea bottom and at mid-depth when the water depth exceeds 6m.

(ii.) If the water depth is between 3m and 6m, two depths: 1m below water surface and 1m above sea bottom

(iii.) If the water depth is less than 3m, 1 sample at mid-depth is taken

Duration: During the course of marine works

Coral Monitoring

Parameters: Presence and coverage of hard and soft corals such as diversity, abundance and health status of the corals in the general area, plus other physical and biological condition at the underwater environment

Frequency: One per week for the first three months of the marine works. If no exceedances are reported during the first three months, the frequency may be reduced to twice every month

Duration: During the course of marine works

Post-Construction Monitoring – Marine Water

- 3.10 Upon the marine works (dredging and HDD pipe installation) completion, 4 weeks of post-construction monitoring would be undertaken in accordance with the *Section 4.8 of EM&A Manual*. The requirements of post-construction monitoring such as the parameter, frequency, location and sampling depth is same as the impact monitoring.

Post-Construction Monitoring – Ecology Monitoring

- 3.11 Following completion of the marine works, post project monitoring should be carried out within two weeks of completion of the marine works (HDD and dredging), and should comprise the same two-tier Rapid Assessment Ecological Assessment (REA) method adopted for the baseline survey.

MONITORING EQUIPMENT

Air Quality Monitoring

- 3.12 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to approve. The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.

Noise Monitoring

- 3.13 Sound level meter in compliance with the *International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1)* specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the wind speed in m/s.

Water Quality Monitoring

- 3.14 **Dissolved Oxygen and Temperature Measuring Equipment** – The instrument should be a portable and weatherproof dissolved oxygen (DO) measuring instrument complete with cable and sensor, and use a DC power source. The equipment should be capable of measuring as included a DO level in the range of 0 – 20mg L⁻¹ and 0 – 200% saturation; and a temperature of 0 – 45 degree Celsius.
- 3.15 **pH Meter** – The instrument shall consist of a potentiometer, a glass electrode, a reference electrode and a temperature-compensating device. It shall be readable to 0.1 pH in arrange of 0 to 14.
- 3.16 **Turbidity (NTU) Measuring Equipment** – The instrument should be a portable and weatherproof turbidity measuring instrument using a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0 - 1000 NTU.
- 3.17 **Water Sampling Equipment** – A water sampler should comprise a transparent PVC cylinder, with a capacity of not less than 2 litres, which can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth.
- 3.18 **Water Depth Detector** – A portable, battery-operated echo sounder should be used for the determination of water depth at each designated monitoring station. This unit can either be hand held or affixed to the bottom of the work boat.
- 3.19 **Salinity Measuring Equipment** – A portable salinometer capable of measuring salinity in the range of 0 - 40 parts per thousand (ppt) should be provided for measuring salinity of the water at each monitoring location.
- 3.20 **Sample Containers and Storage** – Water samples for suspended solids should be stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4°C without being frozen).
- 3.21 **Monitoring Position Equipment** - A hand-held or boat-fixed type digital Differential Global Positioning System (DGPS) with way point bearing indication and Radio Technical Commission for maritime (RTCM) Type 16 error message ‘screen pop-up’ facilities (for real-time auto-display of error messages and DGPS corrections from the Hong Kong Hydrographic Office), or other equipment instrument of similar accuracy, should be provided and used during marine water monitoring to ensure the monitoring vessel is at the correct location before taking measurements.
- 3.22 **Suspended Solids Analysis** – Analysis of suspended solids shall be carried out in a HOKLAS or other international accredited laboratory.

Coral Monitoring

- 3.23 The monitoring equipments used for the coral monitoring could be referred to **Impact Coral Monitoring report** which enclosed in **Appendix M**.

EQUIPMENT CALIBRATION

- 3.24 Calibration of the High Volume Sampler (HVS) is performed upon installation in accordance with the manufacturer’s instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5025A). The calibration data are properly documented and the records are maintained by ET for future reference.
- 3.25 The 1-hour TSP meter was calibrated by the supplier prior to purchase. Zero response of the equipment was checked before and after each monitoring event. In-house calibration with the High Volume Sampler (HVS) in same condition was undertaken in yearly basis.
- 3.26 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.

- 3.27 The water quality monitoring equipments such as DO meter, pH Meter, turbidity measuring instrument and salinometer, are calibrated by HOKLAS accredited laboratory of three month intervals.
- 3.28 All updated calibration certificates of the monitoring equipment used for the impact monitoring programme in the Reporting Period would be attached in *Appendix E*.

METEOROLOGICAL INFORMATION

- 3.29 The meteorological information during the construction phase is obtained from the Wong Chuk Hang Station of the Hong Kong Observatory (HKO) due to it nearly the Project site.

DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.30 The impact monitoring data are handled by the ET's systematic data recording and management, which complies with in-house Quality Management System. Standard Field Data Sheets (FDS) are used in the impact monitoring programme.
- 3.31 The monitoring data recorded in the equipment e.g. 1-hour TSP meter, sound level meter and Multi-parameter Water Quality Monitoring System, are downloaded directly from the equipments at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data. For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

- 3.32 According to the Yung Shue Wan Environmental Monitoring and Audit Manual, the air quality, construction noise, marine water quality and coral monitoring were established, namely Action and Limit levels are listed in *Tables 3-5* to *3-8* as below.

Table 3-5 Action and Limit Levels for Air Quality

Monitoring Station	Action Level ($\mu\text{g}/\text{m}^3$)		Limit Level ($\mu\text{g}/\text{m}^3$)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
AC02b	288	161	500	260
AC04c	290	176	500	260

Table 3-6 Action and Limit Levels for Construction Noise

Recommended Action & Limit Levels of Construction Noise		
Monitoring Location	Action Level	Limit Level
	0700-1900 hours on normal weekdays	
NC05	When one or more documented complaints are received	75 dB(A) *

Note: * Reduces to 70dB(A) for schools and 65dB(A) during the school examination periods.

Table 3-7 Action and Limit Levels for Marine Water Quality

Parameter	Performance Criteria	Impact Station		
		WY1	WY2	WY3
DO Concentration (Surface and Middle) (mg/L)	Action Level	3.63	3.53	3.61
	Limit Level	3.32	3.47	3.42
DO Concentration (Bottom) (mg/L)	Action Level	3.33	2.92	3.36
	Limit Level	3.23	2.63	3.14
Turbidity (Depth-Average) (NTU)	Action Level	10.94	14.16	14.99
	Limit Level	17.35	15.20	16.21

Parameter	Performance Criteria	Impact Station		
		WY1	WY2	WY3
Suspended Solids (Depth-Average) (mg/L)	Action Level	17.52	14.04	14.52
	Limit Level	25.62	16.51	16.88

Table 3-8 Action and Limit Levels for Coral Monitoring

Step	Action
1	Commence tagged coral monitoring at the impact site. If no increase in sedimentation cover/bleaching/partial mortality is observed on the hard corals or partial mortality on the soft/black corals, no action is required. If an increase in sedimentation cover/bleaching/partial mortality is observed on the hard corals or partial mortality on the soft/black corals at one or more impact monitoring stations Step 3 should be enacted, if not, Step 2.
2	If non actions are triggered a formal report should be issued along with evidentiary photographs following completion of the survey. Meanwhile monitoring work and construction works should continue uninterrupted.
3	If during the impact monitoring a 15% increase in the percentage of sedimentation on the hard corals occurs at more than 20% of the tagged coral colonies at the Impact Monitoring Station that is not reported at the Control Monitoring Station, then the Action Level is exceeded (Step 4).
4	If the Action Level is exceeded the IC(E) should inform all parties. The data from the water quality monitoring should also be reviewed. If the water quality monitoring shows no attributable effects of the installation works, then the Action Level is not triggered. If the water quality data indicate exceedances (for SS and/or turbidity) the IC(E) should discuss with the Contractor the most appropriate method of reducing suspended solids during construction (e.g. reduce rate of dredging). The water quality data reviewed should then be enacted on the next working day.
5	Monitoring should proceed the following day as per Step 1. If during the Impact Monitoring a 25% increase in the percentage of sedimentation on the hard corals at more than 20% of the tagged coral colonies at the Impact Monitoring Station that is not reported at the Control Monitoring Station, then the Limit Level is exceeded (Step 6). If the Limit Level is not exceeded Step 2 is enacted and work continues according to the mitigated method.
6	If the Limit Level is exceeded the Inspector Officer should inform all parties immediately. Should the Limit Level be exceeded, the Contractor should stop works immediately and work out a solution to the satisfaction of the IC(E), EPD and AFCD. The IC(E) should inform the Contractor to suspend marine construction works until an effective solution is identified. Once the solution has identified and agreed with all parties, backfilling works may re-commence.

- 3.33 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan enclosed in [Appendix F](#).

4 IMPACT MONITORING RESULTS - AIR QUALITY

4.01 As informed by Leader, the construction of relevant land works at Yung Shue Wan was commenced on 14 September 2010, therefore, the impact EM&A programme was begun as compliance with the contract Particular Specification, Yung Shue Wan EM&A Manual and the EP.

Result

4.02 In this reporting period, the results for 24-hour and 1-hour TSP monitoring are tabulated in *Tables 4-1 and 4-2*. The 24-hour TSP monitoring data are shown in *Appendix G* and the graphical plots are shown in *Appendix H*.

Table 4-1 Summary of 24-hour and 1-hour TSP Monitoring Results at AC02b

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st hour measured	2 nd hour measured	3 rd hour measured
6-Sep-11	32	5-Sep-11	9:26	51	54	59
12-Sep-11	55	9-Sep-11	12:56	71	69	56
17-Sep-11	44	15-Sep-11	10:38	49	58	54
23-Sep-11	153	21-Sep-11	13:08	76	69	64
29-Sep-11	62	26-Sep-11	1:30	92	89	102
Average (Range)	69 (32 – 153)	Average (Range)		68 (49 – 102)		

Table 4-2 Summary of 24-hour and 1-hour TSP Monitoring Results at AC04c

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st hour measured	2 nd hour measured	3 rd hour measured
6-Sep-11	54	5-Sep-11	9:48	61	57	56
12-Sep-11	45	9-Sep-11	13:36	68	53	74
17-Sep-11	25	15-Sep-11	10:12	56	61	59
23-Sep-11	103	21-Sep-11	15:12	69	62	71
29-Sep-11	54	26-Sep-11	1:30	113	105	108
Average (Range)	56 (25 – 103)	Average (Range)		72 (53 – 113)		

4.03 As shown in *Tables 4-1 and 4-2*, the 1-hour TSP monitoring and 24-hour TSP monitoring values fluctuated well below the Action Level during the Reporting Period. No Notification of Exceedance (NOE) of air quality criteria or corrective action was therefore required.

4.04 The meteorological information during the impact monitoring days are summarized in *Appendix I*.

5 IMPACT MONITORING RESULTS – CONSTRUCTION NOISE

5.01 The noise monitoring results are presented in the following sub-sections.

Result

5.02 In this report period, 5 construction noise monitoring events were undertaken at designated location NC05. The results for Leq_{30min} are tabulated in *Tables 5-1* and the graphical plots are shown in *Appendix H*.

Table 5-1 Summarized of Construction Noise Monitoring Results at NC05

Date	Start Time	End Time	1 st set Leq5	2 nd set Leq5	3 rd set Leq5	4 th set Leq5	5 th set Leq5	6 th set Leq5	Leq30	Corrected Leq30*
5-Sep-11	11:04	11:34	51.9	54.7	56.2	54.0	56.9	59.2	56.1	59.1
9-Sep-11	14:28	14:58	57.7	52.3	58.6	54.6	57.3	54.8	56.4	59.4
15-Sep-11	15:51	16:21	64.4	61.8	60.7	60.3	62.9	60.0	62.0	65.0
21-Sep-11	14:38	15:08	56.9	51.2	57.4	54.8	56.3	55.8	55.8	58.8
26-Sep-11	13:35	14:05	64.2	64.8	62.5	61.3	65.5	63.1	63.8	66.8
Limit Level									-	75 dB(A)

* A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

5.03 It was noted that no noise complaint (which is an Action Level exceedance) was received. In view of the results shown in *Tables 5-1*, all the values are well below 75dB(A), therefore, no Action or Limit Level exceedance was triggered during this Reporting Period.

6 IMPACT MONITORING RESULTS – WATER QUALITY

- 6.01 The construction of marine outfall works was commenced on 9 May 2011 and therefore marine water quality monitoring is required in this reporting period. In this reporting period, **14** events of water quality monitoring were carried out at the designated locations. The monitoring results including in-situ measurements and laboratory testing results are presented in *Appendix G*. The graphical plots are shown in *Appendix H*.
- 6.02 During the Reporting Period, field measurements of both control and impact stations showed that marine water of the depth average of the salinity concentration was within **28.28 to 32.83** ppt, and pH value was within **7.60 to 8.28**.
- 6.03 Monitoring results of 3 key parameters: dissolved oxygen (DO), turbidity and suspended solids in this Reporting Period, are summarized in *Tables 6-1, 6-2, 6-3 and 6-4*. A summary of exceedances for the three parameters: dissolved oxygen (DO), turbidity and suspended solids are shown in *Table 6-5*.

Table 6-1 Summary of Water Quality Results – Mid-ebb Tides (Dissolved Oxygen)

Sampling date	Dissolved Oxygen conc. of Depth Ave. of Surf. and Mid Layer (mg/L)					Dissolved Oxygen conc. of Depth Ave. of Bottom Layer (mg/L)				
	WY1	WY2	WY3	CY1	CY2	WY1	WY2	WY3	CY1	CY2
1-Sep-11	6.64	6.51	5.93	6.50	6.31	6.15	6.04	5.69	5.67	5.72
3-Sep-11	6.68	6.82	6.72	6.40	6.36	6.24	6.54	6.60	6.31	6.10
5-Sep-11	6.44	6.36	6.44	5.97	6.47	6.26	6.14	6.23	5.67	6.05
7-Sep-11	6.52	6.28	6.30	6.31	6.73	6.08	6.03	6.15	6.02	6.34
9-Sep-11	7.02	6.70	6.66	6.87	6.49	6.52	6.43	6.89	6.72	7.04
12-Sep-11	5.98	5.90	6.30	5.32	5.80	5.61	5.64	6.04	5.13	5.13
15-Sep-11	6.98	6.93	7.00	6.69	6.75	6.68	6.37	6.69	6.39	6.27
17-Sep-11	5.26	5.15	5.29	5.22	5.30	5.31	5.20	5.32	5.22	5.33
19-Sep-11	5.61	5.25	5.39	5.45	5.49	5.50	4.65	5.44	5.06	5.28
21-Sep-11	5.82	5.51	5.84	5.54	5.55	5.38	5.07	5.64	5.04	5.14
23-Sep-11	5.65	5.44	5.67	5.47	5.47	5.64	5.04	5.70	5.55	5.04
26-Sep-11	5.77	5.59	5.68	5.99	5.83	5.62	5.32	5.43	5.82	5.84
28-Sep-11	5.71	5.64	5.76	5.60	5.70	5.62	5.68	5.67	5.42	5.59
30-Sep-11	5.43	5.51	5.44	5.50	5.48	5.52	5.40	5.49	5.27	5.42

Table 6-2 Summary of Water Quality Results – Mid-ebb Tides (Turbidity & Suspended Solids)

Sampling date	Turbidity Depth Ave. (NTU)					Suspended Solids Depth Ave. (mg/L)				
	WY1	WY2	WY3	CY1	CY2	WY1	WY2	WY3	CY1	CY2
1-Sep-11	2.98	3.38	2.88	2.88	3.35	5.50	4.13	3.00	3.47	4.67
3-Sep-11	3.08	3.07	3.03	3.07	2.68	4.75	6.80	4.05	4.47	4.50
5-Sep-11	3.53	3.23	3.05	3.25	2.87	7.10	2.57	3.45	2.70	2.83
7-Sep-11	3.46	3.33	4.31	3.72	3.40	5.70	7.57	6.25	6.47	7.63
9-Sep-11	4.59	4.39	4.56	4.13	4.49	9.45	8.83	10.60	7.03	4.53
12-Sep-11	5.83	4.77	5.86	5.44	7.50	8.30	9.77	8.15	6.07	3.03
15-Sep-11	4.04	4.03	4.23	3.57	3.78	16.85	8.03	7.90	4.20	4.70
17-Sep-11	3.24	4.19	4.22	4.07	5.80	6.80	7.73	6.55	5.23	6.63
19-Sep-11	4.08	3.74	5.96	5.92	7.17	8.45	6.87	9.60	8.20	8.37
21-Sep-11	4.23	4.49	7.47	6.79	5.74	7.85	8.17	11.50	7.57	6.37
23-Sep-11	6.75	3.83	4.55	4.94	7.11	15.25	6.83	7.15	5.90	6.87
26-Sep-11	6.13	5.71	3.71	13.55	12.77	13.80	10.40	5.85	16.13	12.33
28-Sep-11	3.83	3.98	3.48	6.39	9.06	11.00	7.47	12.05	9.20	8.77
30-Sep-11	4.10	4.20	4.04	4.46	4.64	5.80	8.90	9.05	9.73	16.90

Table 6-3 Summary of Water Quality Results – Mid-flood Tides (Dissolved Oxygen)

Sampling date	Dissolved Oxygen conc. of Depth Ave. of Surf. and Mid Layer (mg/L)					Dissolved Oxygen conc. of Depth Ave. of Bottom Layer (mg/L)				
	WY1	WY2	WY3	CY1	CY2	WY1	WY2	WY3	CY1	CY2
1-Sep-11	6.81	6.95	6.30	7.00	6.66	6.30	6.70	5.64	6.67	5.73
3-Sep-11	6.80	6.90	6.24	6.19	6.88	6.27	6.47	6.72	6.18	6.49
5-Sep-11	6.28	6.78	6.40	6.37	6.48	6.09	6.53	6.09	5.92	6.25
7-Sep-11	6.18	6.83	6.49	6.44	6.40	6.01	6.30	6.24	5.39	5.84
9-Sep-11	6.14	6.55	6.20	6.66	6.48	6.42	5.87	6.29	6.51	5.99
12-Sep-11	6.08	5.81	5.97	6.00	6.08	6.02	5.57	5.79	5.80	5.91
15-Sep-11	6.91	6.95	6.93	6.62	6.91	6.57	6.77	6.49	6.24	6.76
17-Sep-11	4.98	5.47	6.94	5.17	4.91	4.33	5.30	4.96	4.99	5.00
19-Sep-11	5.32	5.68	5.55	4.78	4.62	4.52	5.07	4.85	4.74	4.67
21-Sep-11	5.31	5.93	5.38	5.53	5.36	5.66	5.39	5.71	5.25	4.96
23-Sep-11	5.60	5.62	5.49	5.48	5.61	5.30	5.30	5.64	5.60	5.55
26-Sep-11	5.83	5.80	5.79	5.60	5.87	5.77	5.78	5.85	5.29	5.42
28-Sep-11	5.55	5.48	5.58	5.78	5.67	5.57	5.61	5.59	5.53	5.53
30-Sep-11	5.64	5.45	5.76	5.60	5.52	5.52	5.18	5.27	5.21	5.32

Table 6-4 Summary of Water Quality Results – Mid-flood Tides (Turbidity & Suspended Solids)

Sampling date	Turbidity Depth Ave. (NTU)					Suspended Solids Depth Ave. (mg/L)				
	WY1	WY2	WY3	CY1	CY2	WY1	WY2	WY3	CY1	CY2
1-Sep-11	3.18	2.75	2.85	3.42	3.63	4.70	3.73	3.55	7.40	4.43
3-Sep-11	3.20	2.87	3.20	2.88	2.95	7.20	5.67	13.10	6.87	5.50
5-Sep-11	2.86	2.76	3.10	2.99	3.24	4.90	5.93	3.35	3.53	8.67
7-Sep-11	3.40	3.27	3.22	3.45	4.42	10.90	5.07	8.40	4.03	4.40
9-Sep-11	4.47	4.02	3.89	4.83	4.33	7.55	4.50	3.90	4.77	5.13
12-Sep-11	5.67	4.72	6.07	7.73	6.32	4.95	5.03	4.70	4.37	4.73
15-Sep-11	3.48	3.95	4.39	4.12	4.49	4.65	4.77	3.15	4.37	5.87
17-Sep-11	5.12	6.59	6.63	9.49	6.66	8.75	9.30	9.40	12.30	9.40
19-Sep-11	7.62	5.12	8.23	7.32	5.79	8.50	7.03	10.65	7.57	7.57
21-Sep-11	4.44	8.34	5.99	5.64	5.38	7.45	11.47	7.15	6.40	7.00
23-Sep-11	6.35	6.30	9.25	8.21	7.19	8.20	8.30	10.35	8.43	8.70
26-Sep-11	7.91	8.55	10.77	14.94	10.86	10.10	11.30	12.05	15.50	13.10
28-Sep-11	6.43	5.16	7.86	9.90	4.09	8.00	9.00	9.30	8.17	7.33
30-Sep-11	4.32	4.10	3.92	4.58	4.75	14.50	8.63	11.70	20.87	21.17

Table 6-5 Summarized Exceedances of Marine Water Quality

Station	DO (Ave of Surf. & mid-depth)		DO (Ave. of Bottom Layer)		Turbidity (Depth Ave.)		SS (Depth Ave)		Total Exceedance	
	Action	Limit	Action	Limit	Action	Limit	Action	Limit	Action	Limit
Mid-Ebb										
WY1	0	0	0	0	0	0	0	0	0	0
WY2	0	0	0	0	0	0	0	0	0	0
WY3	0	0	0	0	0	0	0	0	0	0
Mid-Flood										
WY1	0	0	0	0	0	0	0	0	0	0
WY2	0	0	0	0	0	0	0	0	0	0
WY3	0	0	0	0	0	0	0	0	0	0
No of Exceedance	0	0	0	0	0	0	0	0	0	0

6.04 For marine water monitoring, no exceedance of Action/Limit level was recorded in this Reporting Period. Therefore, no associated corrective actions were then required.

7 IMPACT MONITORING RESULTS – ECOLOGY MONITORING

- 7.01 Impact monitoring for coral shall be conducted initially at a frequency of once per week for the first three months of the marine works (HDD and dredging). If no exceedances are reported during this period, then the frequency may be reduced to twice every month for the remainder of the marine works.
- 7.02 According to the EM&A Manual [*Appendix D of the Review Report on EIA Study – Yung Shue Wan (Final) in January 2007*] Section 7.3.1, if no exceedances are reported during first three month, then the frequency may be reduced to twice every month for the remainder of the marine works. In view of the monitoring results at the first three months (since marine work commenced on 9 May 2011), no adverse deterioration of the coral community was observed and identified by the marine ecologist. However, coral partial mortality which no related to the Project was occasionally reported. As advised by the ER and IEC, the coral impact monitoring would be remain at once per week in September and October to closely monitor the condition of the coral.
- 7.03 In this Reporting Period, impact coral monitoring have been conducted on **9, 15, 22 and 28 September 2011** by the marine ecologist. The impact coral monitoring report for this Reporting Period is presented in *Appendix M*.

8 WASTE MANAGEMENT

8.01 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

Records of Waste Quantities

8.02 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) material;
- Chemical waste;
- General refuse; and
- Excavated soil.

8.03 The quantities of waste for disposal in this Reporting Period are summarized in *Tables 8-1* and *8-2* and the Monthly Summary Waste Flow Table is shown in *Appendix J*. Whenever possible, materials were reused on-site as far as practicable

Table 8-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
C&D Materials (Inert) ('000m ³)	0.037	Tuen Mun Area 38
Reused in this Contract (Inert) ('000m ³)	0	-
Reused in other Projects (Inert) ('000m ³)	0	-
Disposal as Public Fill (Inert) ('000m ³)	0.074	Tuen Mun Area 38

Table 8-2 Summary of Quantities of C&D Wastes

Type of Waste	Quantity	Disposal Location
Recycled Metal (kg)	0	-
Recycled Paper / Cardboard Packing (kg)	0	-
Recycled Plastic (kg)	0	-
Chemical Wastes (kg)	0	-
General Refuses (tonne)	23.03	Yung Shue Wan RTS

8.04 There was no site effluent discharged but the estimated volume of surface runoff was less than 50m³ in this monthly period.

9 SITE INSPECTION

- 9.01 According to the Environmental Monitoring and Audit Manual, the environmental site inspection should be formulated by ET Leader. Regular environmental site inspections had been carried out by the ET to confirm the environmental performance. In this reporting period, weekly site inspection by ET was carried out on **6, 14, 20 and 27 September 2011** and a joint-site visit by IEC Representative, RE, Leader and ET was carried out on **20 September 2011**.
- 9.02 The findings/ deficiencies that observed during the weekly site inspection are listed in **Table 9-1** and the relevant checklists are attached in **Appendix K**.

Table 9-1 Site Observations

Date	Findings / Deficiencies	Follow-Up Status
6 September 2011	<ul style="list-style-type: none">There is no geotextile sheets installed in the sedimentation tank. The contractor should install them to restore desilting functioning.	Geotextile sheets were installed on 14 September 2011.
14 September 2011	<ul style="list-style-type: none">No environmental issue was observed during the site inspection.	N.A.
20 September 2011	<ul style="list-style-type: none">No environmental issue was observed during the site inspection.	N.A.
27 September 2011	<ul style="list-style-type: none">No environmental issue was observed during the site inspection.	N.A.

10 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

10.01 No environmental complaint, summons and prosecution was received in this reporting period. The statistical summary table of environmental complaint is presented in *Tables 10-1, 10-2* and *10-3*.

Table 10-1 Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
14 Sep – 30 June 2011	0	0	NA
1 – 31 July 2011	0	0	NA
1 – 31 August 2011	0	0	NA
1 – 30 September 2011	0	0	NA

Table 10-2 Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Complaint Nature
14 Sep – 30 June 2011	0	0	NA
1 – 31 July 2011	0	0	NA
1 – 31 August 2011	0	0	NA
1 – 30 September 2011	0	0	NA

Table 10-3 Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Complaint Nature
14 Sep – 30 June 2011	0	0	NA
1 – 31 July 2011	0	0	NA
1 – 31 August 2011	0	0	NA
1 – 30 September 2011	0	0	NA

11 IMPLEMENTATION STATUS OF MITIGATION MEASURES

11.01 The environmental mitigation measures that recommended in the Yung Shue Wan Environmental Monitoring and Audit Manual covered the issues of dust, noise, water and waste and they are summarized as following:

Dust Mitigation Measure

11.02 Installation of 2m high solid fences around the construction site of Pumping Station P2 is recommended. Implementation of the requirements stipulated in the Air Pollution Control (Construction Dust) Regulation and the following good site practices are recommended to control dust emission from the site:

- Stockpiles of imported material kept on site should be contained within hoardings, dampened and / or covered during dry and windy weather;
- Material stockpiled alongside trenches should be covered with tarpaulins whenever works are close to village houses;
- Water sprays should be used during the delivery and handling of cement, sands, aggregates and the like.
- Any vehicle used for moving sands, aggregates and construction waste shall have properly fitting side and tail boards. Materials should not be loaded to a level higher than the side and tail boards, and should be covered by a clean tarpaulin.

Noise Mitigation Measure

11.03 As detailed in the EIA report, concreting work of the Pumping Station P1a and sewer alignment construction activities would likely cause adverse noise impacts on some of the noise sensitive receivers. Appropriate mitigation measures have therefore been recommended. The mitigation measures recommended in the EIA report are summarised below:

- (a) Use of quiet equipment for the construction activities of the Pumping Stations and sewer alignment;
- (b) Use of temporary noise barrier around the site boundary of Pumping Station P1a;
- (c) Use of kick ripper (saw and lift) method to replace the breaker for pavement removal during sewer alignment construction;
- (d) Restriction on the number of plant during sewer alignment construction;
- (e) Use of noise screening structures in the form of acoustic shed or movable barrier wherever practicable and feasible in areas with sufficient clearance and headroom during the construction of sewer alignment;
- (f) Adoption of manual working method wherever practicable and feasible in areas where the worksites of the proposed sewer alignment are located less than 20m from the residential noise sensitive receivers and less than 30m from the temple and the public library; and
- (g) Implementation of the following good site practices:
 - Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme.
 - Mobile plant, if any, should be sited as far away from NSRs as possible.
 - Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.
 - Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.
 - Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.

Water Quality Mitigation Measure

11.04 No-dig method using Horizontal Directional Drilling (HDD) would be used for the installation of outfall pipe of about 480 m from shore to minimize the potential water quality impacts arising from the dredging works required for the submarine outfall construction. For the remaining outfall pipe of about 240m and the diffuser section, open trench dredging would still be required.

- 11.05 During the dredging works, the Contractor should be responsible for the design and implementation of the following mitigation measures.
- Dredging should be undertaken using closed grab dredgers with a total production rate of 55m³/hr;
 - Deployment of 2-layer silt curtains with first layer enclosing the grab and the second layer at around 50, from the dredging area while dredging works are in progress;
 - all vessels should be sized such that adequate clearance (i.e. minimum clearance of 0.6m) is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;
 - all pipe leakages should be repaired promptly and plant shall not be operated with leaking pipes;
 - excess material should be cleaned from the decks and exposed fittings of barges before the vessel is moved;
 - adequate freeboard (i.e. minimum of 200m) should be maintained on barges to ensure that decks are not washed by wave action;
 - all barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; and
 - loading of barges and hoppers should be controlled to prevent splashing of dredged material to the surrounding water, and barges and hoppers should not be filled to a level which would cause the overflow of materials or sediment laden water during loading or transportation; and
 - the decks of all vessels should be kept tidy and free of oil or other substances that might be accidentally or otherwise washed overboard.

Construction Run-off and Drainage

- 11.06 The Contractor should observe and comply with the Water Pollution Control Ordinance and the subsidiary regulations. The Contractor should follow the practices, and be responsible for the design, construction, operation and maintenance of all the mitigation measures as specified in ProPECC PN 1/94 “Construction Site Drainage”. The design of the mitigation measures should be submitted by the Contractor to the Engineer for approval. These mitigation measures should include the following practices to minimise site surface runoff and the chance of erosion, and also to retain and reduce any suspended solids prior to discharge:
- Provision of perimeter channels to intercept storm-runoff from outside the site. These should be constructed in advance of site formation works and earthworks.
 - Works programmes should be designed to minimize works areas at any one time, thus minimising exposed soil areas and reducing the potential for increased siltation and runoff.
 - Sand/silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove the sand/silt particles from run-off. These facilities should be properly and regularly maintained. These facilities shall be carefully planned to ensure that they would be installed at appropriate locations to capture all surface water generated on site.
 - Careful programming of the works to minimise soil excavation works during rainy seasons.
 - Exposed soil surface should be protected by paving or hydroseeding as soon as possible to reduce the potential of soil erosion.
 - Trench excavation should be avoided in the wet season, and if necessary, these should be excavated and backfilled in short sections.
 - Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric.

General Construction Activities

- 11.07 Debris and rubbish generated on-site should be collected, handled and disposed of properly to avoid entering the nearby coastal waters and stormwater drains. All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Open drainage channels and culverts near the works areas should be covered to block the entrance of large debris and refuse.

Wastewater Arising from Workforce

- 11.08 Portable toilets shall be provided by the Contractors, where necessary, to handle sewage from the workforce. The Contractor shall also be responsible for waste disposal and maintenance practices

Sediment Contamination Mitigation Measure

- 11.09 The basic requirements and procedures for dredged mud disposal are specified under the WBTC No. 34/2002. The management of the dredging, use and disposal of marine mud is monitored by the MFC, while the licensing of marine dumping is the responsibility of the Director of Environmental Protection (DEP).
- 11.10 The uncontaminated dredged sediment will be loaded onto barges and transported to the designated marine disposal site. Appropriate dredging methods have been incorporated into the recommended water quality mitigation measures including the use of closed-grab dredgers and silt curtains. Category L sediment would be suitable for disposal at a gazetted open sea disposal ground.
- 11.11 During transportation and disposal of the dredged marine sediments, the following measures should be taken to minimize potential impacts on water quality:
- Bottom opening of barges should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.
 - Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self-monitoring devices as specified by the DEP.

Construction Waste Mitigation Measure

Good Site Practices and Waste Reduction Measures

- 11.12 It is not anticipated that adverse waste management related impacts would arise, provided that good site practices are strictly followed. Recommendations for good site practices for the construction waste arising include:
- Nomination of an approved person, such as a site manager, to be responsible for the implementation of good site practices, arranging for collection and effective disposal to an appropriate facility, of all wastes generated at the site.
 - Training of site personnel in proper waste management and chemical handling procedures.
 - Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.
 - Provision of sufficient waste disposal points and regular collection for disposal.
 - Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility.
 - Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.
 - Maintain records of the quantities of wastes generated, recycled and disposed.
- 11.13 In order to monitor the disposal of C&D waste at landfills and to control fly tipping, a trip-ticket system should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.
- 11.14 Good management and control can prevent the generation of significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:
- segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;

- to encourage collection of aluminium cans by individual collectors, separate labelled bins should be provided to segregate this waste from other general refuse generated by the work force;
- any unused chemicals or those with remaining functional capacity should be recycled;
- use of reusable non-timber formwork to reduce the amount of C&D material;
- prior to disposal of C&D waste, it is recommended that wood, steel and other metals should be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill;
- proper storage and site practices to minimise the potential for damage or contamination of construction materials; and
- plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.

General Site Wastes

- 11.15 A collection area should be provided where waste can be stored prior to removal from site. An enclosed and covered area is preferred for the collection of the waste to reduce 'wind blow' of light material.

Chemical Wastes

- 11.16 After use, chemical waste (eg. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Any unused chemicals or those with remaining functional capacity should be recycled. Spent chemicals should be properly stored on site within suitably designed containers, and should be collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licenced facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation under the Waste Disposal Ordinance.
- 11.17 Any service shop and minor maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakages and spillage should only be undertaken with the areas appropriately equipped to control these discharges.

Construction and Demolition Material

- 11.18 The C&D material should be separated on-site into three categories: (i) public fill, the inert portion of the C&D material (e.g. concrete and rubble), which should be re-used on-site or disposed of at a public filling area; (ii) C&D waste for re-use and/or recycling, the non-inert portion of the C&D material, (e.g. steel and other metals, wood, glass and plastic); (iii) C&D waste which cannot be re-used and/or recycled. The waste producers are responsible for its disposal at strategic landfills.
- 11.19 In order to minimise the impact resulting from collection and transportation of material for off-site disposal, it was recommended that inert material should be re-used on-site where possible. Prior to disposal of C&D material, it was also recommended that steel and other metals should be separated for re-use and/or recycling where practicable to minimise the quantity of waste to be disposed of to landfill.

Ecology Mitigation Measure

- 11.20 The following general good practice measures should be adopted to mitigate ecological impacts during marine works (including dredging and HOD);
- Excess material from vessel loading should be cleaned from the decks and exposed fittings before vessels are moved to the backfilling location;
 - Dredging should cause no foam, oil, grease, scum, litter or other objectionable matter to be present on the water;
 - Adequate freeboard should be maintained to ensure that decks are not washed by wave action;
 - All pie leakages should be repaired promptly and plant Should not be operated with leaking pipes; and

- All barges and other vessels should maintain adequate clearance between vessels and the seabed at all states of the tide and reduce operational speeds to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash.
- 11.21 In the event of exceedances of ecological action or limit level, the Contractor will be required to revise his operations as a further mitigation measure. Revisions to the operation method may include (but not be limited to):
- Reduction in dredging rate
 - Restriction of dredging in particular areas to specific periods in the tidal cycle
- 11.22 Should repeated non-compliances with limit level(s) occur the Contractor shall modify his working method until he is able to achieve the required compliances with the limit levels to the satisfaction of the IC(E)

Fisheries Mitigation Measure

- 11.23 Closed grab dredger, deployment of silt curtains around the immediate dredging area and low dredging rate have been recommended in Water Quality of the EIA report in order to minimise sediment release into the water column.

Landscape & Visual Mitigation Measure

- 11.24 Mitigation measures recommended in the EIA Report for landscape and visual impacts during the construction stage are summarised below.
- Screening of site construction works by use of hoarding that is appropriate to its site context;
 - Retaining existing trees and minimising damage to vegetation where possible by close co-ordination and on site alignment adjusted of rising main and gravity sewer pipelines. Tree protective measures should be implemented to ensure trees identified as to be retained are satisfactorily protected during the construction phase;
 - Careful and efficient transplanting of affected trees (1 no.) to temporary or final transplant location (the proposed tree to be transported is a semi-mature *Macaranga tanarius* and is located at the proposed Pumping Station P2 location);
 - Short excavation and immediate backfilling of sections upon completion of works to reduce active site area;
 - Conservation of top-soil for reuse;
 - Night-time light source from marine fleets should be directed away from the residential units
- 11.25 The implementation schedule of mitigation measures is presented in [Appendix L](#).
- 11.26 Leader had been implementing the required environmental mitigation measures according to the Yung Shue Wan Environmental Monitoring and Audit Manual subject to the site condition. Environmental mitigation measures generally implemented by Leader in this Reporting Period are summarized in [Table 11-1](#).

Table 11-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> • Drainage channels were provided to convey run-off into the treatment facilities; and • Drainage systems were regularly and adequately maintained.
Air Quality	<ul style="list-style-type: none"> • Cover all excavated or stockpile of dusty material by impervious sheeting or sprayed with water to maintain the entire surface wet; • Public roads around the site entrance/exit had been kept clean and free from dust; and • Tarpaulin covering of any dusty materials on a vehicle leaving the site.

Issues	Environmental Mitigation Measures
Noise	<ul style="list-style-type: none">• Good site practices to limit noise emissions at the sources;• Use of quiet plant and working methods;• Use of site hoarding or other mass materials as noise barrier to screen noise at ground level of NSRs; and• To minimize plant number use at the worksite.
Waste and Chemical Management	<ul style="list-style-type: none">• Excavated material should be reused on site as far as possible to minimize off-site disposal. Scrap metals or abandoned equipment should be recycled if possible;• Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner;• The Contractor should adopt a trip ticket system for the disposal of C&D materials to any designed public filling facility and/or landfill; and• Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.
General	<ul style="list-style-type: none">• The site was generally kept tidy and clean.

12 IMPACT FORECAST

12.01 Key issues to be considered in the coming month include:

Water Quality

- Erect of sand bag in proper area to avoid any muddy surface runoff from the loose soil surface or haul road during the rainy days; and
- The accumulated stagnant water should be drained away.

Air Quality

- Vehicles shall be cleaned of mud and debris before leaving the site;
- Stockpile and loose soil surface shall be covered with tarpaulin sheet or other means to eliminate the fugitive dust;
- Water spaying on the dry haul road and exit/entrance of the site in regular basis is reminded; and
- Public roads around the site entrance/exit had been kept clean and free from dust.

Noise

- Works and equipment should be located to minimize noise nuisance from the nearest sensitive receiver; and
- Idle equipments should be either turned off or throttled down;

Waste and Chemical Management

- Housekeeping on site shall be improved;
- The Contractor is advised to fence off the construction waste at a designated area in order to maintain the tidiness of the site;
- Drip tray and proper label should be provided for all chemical containers.
- C&D waste should be disposed in regular basis.

13 CONCLUSIONS AND RECOMMENDATIONS

CONCLUSIONS


- 13.01 This is the **13th** Monthly EM&A Report covering the construction period from **1 to 30 September 2011**.
- 13.02 No 1-hour TSP and 24-TSP monitoring result was found to be triggered the Action or Limit Level in this Reporting Period.
- 13.03 No noise complaint (an Action Level exceedance) was received and no construction noise measurement results that exceeded the Limit Level were recorded in this Reporting Period.
- 13.04 No exceedance of Action/Limit level was recorded in marine water monitoring in this Reporting Period.
- 13.05 No exceedance of Action/Limit level was recorded in coral monitoring in this Reporting Period.
- 13.06 No documented complaint, notification of summons or successful prosecution was received.
- 13.07 In this reporting period, weekly site inspection by ET was carried out on **6, 14, 20 and 27 September 2011**. Besides, a joint-site visit by IEC Representative, RE, Leader and ET was carried out on **20 September 2011**. All the observation has been rectified during the next week site inspection. The environmental performance of the Project was therefore considered as satisfactory.

RECOMMENDATIONS

- 13.08 During wet season, the Contractor shall pay attention on the potential water impact as the construction site is adjacent to the coastline. Muddy water and other water quality pollutants via site surface water runoff into the coral zones of Yung Shue Wan seawall, Shek Kok Tsui and O Tsai should be avoided. Therefore, mitigation measures for water quality should be fully implemented.
- 13.09 Moreover, the construction dust mitigation measures identified at the EM&A Manuel such as watering at haul road and covering of dusty material should also be implemented and properly maintained in wet season.

Appendix A

Site Layout Plan – Yung Shue Wan Portion Area

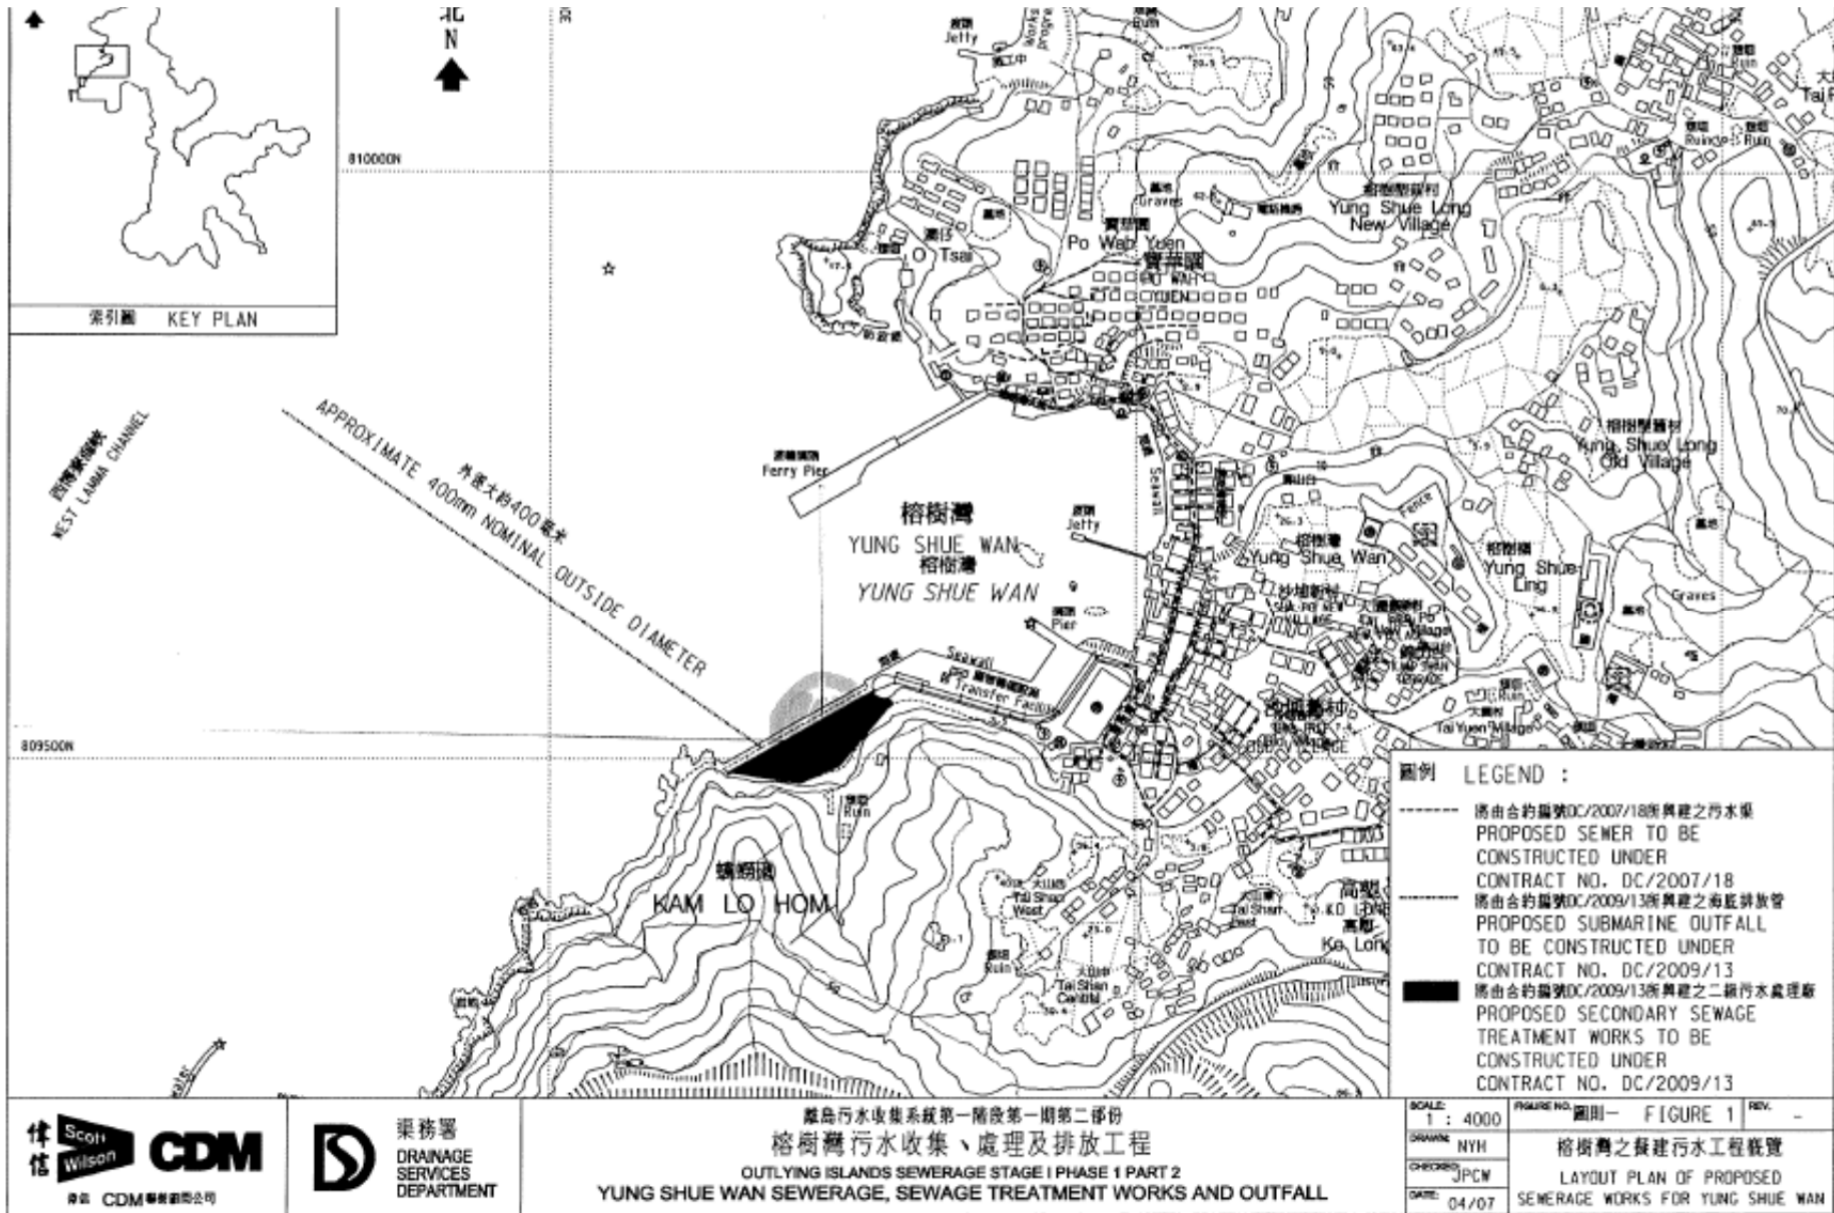

Appendix B

Organization Structure and Contact Details of Relevant Parties

Contact Details of Key Personnel

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
DSD	Employer	Mr. AU Chi Kwong	-	-
SCJV	Engineer's Representative	Mr. Neil Wong	2982 0240	2982 4129
SCJV	Resident Engineer (Yung Shue Wan Portion Area)	Mr. Alfred Cheung	2982 0240	2982 4129
Scott Wilson	Independent Environmental Checker	Mr. Rodney Ip	2410 3750	2428 9922
Leader	Project Manager	Mr. Vincent Chan	2982 1750	2982 1163
Leader	Site Agent	Mr. Stephen Leung	2982 1750	2982 1163
Leader	Environmental Officer	Mr. K.Y. So	2982 8652	2982 8650
Leader	Section Engineer (Yung Shue Wan)	Mr. Burgess Yip	2982 1750	2982 1163
Leader	Site Engineer (Yung Shue Wan)	Mr. Justin Cheng	2982 1750	2982 1163
Leader	Safety Officer	Mr. Edwin Leung	2982 1750	2982 1163
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959 6059	2959 6079
AUES	Assistance Environmental Consultant	Mr. Ray Cheung	2959 6059	2959 6079
AUES	Team Supervisor	Mr. Ben Tam	2959 6059	2959 6079

Legend:

DSD (Employer) – Drainage Services Department

CDM (Engineer) – Scott Wilson CDM Joint Venture

Leader (Main Contractor) – Leader Civil Engineering Corporation Limited

Scott Wilson (IEC) – Scott Wilson Limited

AUES (ET) – Action-United Environmental Services & Consulting

Appendix C

A Master and Three Months Rolling Construction Programme

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2011						
											MAY	JUN	JUL	AUG	SEP	OCT	NOV
Project Key Date																	
KD0010	Receive Letter of Acceptance	0	100		05/05/10 A		05/05/10 A			KD0125							
KD0020	Project Commencement Date	0	100		17/05/10 A		17/05/10 A			E&M0010, E&M0070, E&M1001,							
KD0050	Section W3 - Footpath Diversion in Ptn G (273d)	0	100		24/03/11 A		24/03/11 A		SKW0551	KD0125							
KD0115	Start Operate Temp Sewage Treatment in Port. A&H	0	0		01/12/11		30/06/11 *	-154d *	E&M0510	KD0125							
Preliminary (Civil)																	
PRE0020	Pre-condition Survey	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A		KD0020								
PRE0040	Erection of Engineer's Site Accommodation at YSW	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A		KD0020								
PRE0050	Taking over the Secondary Engineer's Site Accom	75	100	17/05/10 A	30/07/10 A	17/05/10 A	30/07/10 A		KD0020								
PRE0060	Application of Consent from Marine Department	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A		KD0020								
PRE0090	Working Group Meeting for Outfall Construction	120	100	17/05/10 A	23/11/10 A	17/05/10 A	23/11/10 A		KD0020	SKW1151							
PRE0100	Application & Consent of XP from HyD (Mo Tat Rd)	120	100	17/05/10 A	13/10/10 A	17/05/10 A	13/10/10 A		KD0020	SKW1491, SKW1501							
PRE0130	Setup Web-site for EM&A Reporting	90	100	17/05/10 A	31/08/10 A	17/05/10 A	31/08/10 A		KD0020								
Preliminary (E&M)																	
Technical Submission																	
Process Design of SKWSTW & YSWSTW																	
E&M0010	Submission	38	100	17/05/10 A	23/06/10 A	17/05/10 A	23/06/10 A		KD0020	E&M0020, E&M0040, E&M0235							
E&M0020	Vetting and Comment by ER	21	100	24/06/10 A	14/07/10 A	24/06/10 A	14/07/10 A		E&M0010	E&M0030, E&M0040							
E&M0030	Revision and Resubmission	125	98	17/05/10 A	02/08/11	17/05/10 A	16/06/11	-47d	E&M0020	E&M0080							
E&M0080	Approval from the Engineer	14	0	02/08/11	16/08/11	17/06/11	30/06/11	-47d	E&M0030	E&M0295							
Hydraulic Design																	
E&M0040	Submission	21	100	17/05/10 A	16/09/10 A	17/05/10 A	16/09/10 A		E&M0010, E&M0020	E&M0050, E&M0101, E&M0240,							
E&M0050	Vetting and Comment by ER	14	100	17/09/10 A	09/11/10 A	17/09/10 A	09/11/10 A		E&M0040	E&M0060							
E&M0060	Revision and Resubmission	97	95	19/08/10 A	04/08/11	19/08/10 A	28/06/11	-38d	E&M0050	E&M0430							
E&M0430	Approval from the Engineer	7	60	29/03/11 A	07/08/11	29/03/11 A	30/06/11	-38d	E&M0060	E&M0295							
Equipment Submission & Approval																	
E&M0070	Submission of Membrane Module	50	100	17/05/10 A	05/07/10 A	17/05/10 A	05/07/10 A		KD0020	E&M0090							
E&M0090	Vetting and Comment by ER	14	100	06/07/10 A	19/07/10 A	06/07/10 A	19/07/10 A		E&M0070	E&M0100							
E&M0100	Revision and Resubmission	14	100	20/07/10 A	24/02/11 A	20/07/10 A	24/02/11 A		E&M0090	E&M0160							
E&M0101	Submission of Equipment	90	95	04/08/10 A	04/08/11	04/08/10 A	15/02/11	-170d	E&M0040	E&M0102							
E&M0102	Vetting and Comment by ER	60	95	18/11/10 A	07/08/11	18/11/10 A	18/02/11	-170d	E&M0101	E&M0103							
E&M0103	Revision and Resubmission	60	80	01/02/11 A	19/08/11	01/02/11 A	02/03/11	-170d	E&M0102	E&M0110, E&M0120, E&M0130,							
E&M0110	Approval on Coarse Screens	30	100	25/05/11 A	25/05/11 A	25/05/11 A	25/05/11 A		E&M0103	E&M0390							
E&M0120	Approval on Fine Screens	30	0	19/08/11	18/09/11	29/04/11	28/05/11	-113d	E&M0103	E&M0400, E&M3060							
E&M0130	Approval on Pumps	30	0	19/08/11	18/09/11	03/03/11	01/04/11	-170d	E&M0103	E&M0410, E&M3070							
E&M0140	Approval on Submersible Mixers	30	100	23/03/11 A	23/03/11 A	23/03/11 A	23/03/11 A		E&M0103	E&M0420, E&M3080							
E&M0150	Approval on Grit Removal Equipment	30	0	19/08/11	18/09/11	29/04/11	28/05/11	-113d	E&M0103	E&M0380, E&M3030							
E&M0160	Approval on MBR Membrane Modules (M.M.)	105	100	02/08/10 A	24/02/11 A	02/08/10 A	24/02/11 A		E&M0100	E&M0360, E&M0370, E&M3010							
E&M0170	Approval on Sludge Dewatering Equipment	30	0	19/08/11	18/09/11	03/03/11	01/04/11	-170d	E&M0103	E&M0440, E&M3090							
E&M0180	Approval on Valves, Pipes & Fittings	30	0	19/08/11	18/09/11	28/06/11	27/07/11	-53d	E&M0103	E&M0450, E&M3100							
E&M0190	Approval on Penstocks	30	0	19/08/11	18/09/11	11/06/11	10/07/11	-70d	E&M0103	E&M0460, E&M3110							
E&M0200	Approval on Instrumentation	30	0	19/08/11	18/09/11	09/10/11	07/11/11	51d	E&M0103	E&M0470, E&M3130							
E&M0210	Approval on MCC & LVSB	30	0	19/08/11	18/09/11	03/03/11	01/04/11	-170d	E&M0103	E&M0480, E&M3140							
E&M0220	Approval on BS Equipment	30	0	30/08/11	28/09/11	31/07/11	29/08/11	-30d	E&M0103, E&M0280	E&M0490, E&M3150							
E&M0230	Approval on FS Equipment	30	0	30/08/11	28/09/11	01/06/11	30/06/11	-90d	E&M0103, E&M0290	E&M0295, E&M0320, E&M0500,							
Drawings Submission & Approval																	
E&M0235	Sub. P&ID Drawings	100	100	24/06/10 A	22/08/10 A	24/06/10 A	22/08/10 A		E&M0010								
E&M0240	Sub. Plant GA Drawings	45	90	04/08/10 A	04/08/11	04/08/10 A	30/06/11	-35d	E&M0040	E&M0250, E&M0280, E&M0290							
E&M0250	Sub. Builder's Works Requirements Drawings	15	90	04/08/10 A	10/08/11	04/08/10 A	01/07/11	-40d	E&M0240, E&M0260, E&M0270	E&M0280, E&M0290							
E&M0260	Sub. Mechanical Installation Drawings	60	85	27/09/10 A	08/08/11	27/09/10 A	30/06/11	-40d	E&M0040	E&M0250							
E&M0270	Sub. Electrical Installation Drawings	60	85	27/09/10 A	08/08/11	27/09/10 A	30/06/11	-40d	E&M0040	E&M0250, E&M0280							
E&M0280	Sub. BS Installation Drawings	120	75	27/09/10 A	29/08/11	27/09/10 A	30/07/11	-30d	E&M0240, E&M0250, E&M0270	E&M0220							
E&M0290	Sub. FS Installation Drawings	120	75	13/11/10 A	29/08/11	13/11/10 A	31/05/11	-90d	E&M0240, E&M0250	E&M0230							
Statutory Submission																	
E&M0295	Preparation of Submission to HEC	39	0	29/09/11	06/11/11	01/07/11	08/08/11	-90d	E&M0080, E&M0230, E&M0430	E&M0300							

Start date	05/05/10	Early bar
Finish date	13/03/15	Progress bar
Data date	31/07/11	Critical bar
Run date	08/08/11	Summary bar
Page number	1A	Progress point
		Critical point
		Summary point
		Start milestone point
		Finish milestone point

Leader Civil Engineering Corp. Ltd.
 Contract No. DC/2009/13
 Construction of Sewage Treatment Works at YSW & SKW
 3-month Rolling Programme (Aug 2011 - Oct 2011)

(Marked on 31 Jul 2011)

Date	Revision	Checked	Approved
31/07/10	Revision 0	StL	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2011							
											MAY	JUN	JUL	AUG	SEP	OCT	NOV	
E&M0300	Application & Approval from HEC	150	0	07/11/11	04/04/12	09/08/11	05/01/12	-90d	E&M0295	E&M0305								
E&M0320	Form 314 Submission to FSD	14	0	29/09/11	12/10/11	15/04/12	28/04/12	199d	E&M0230	E&M0325, E&M0670								
E&M0325	Submission to WSD	14	0	13/10/11	26/10/11	29/04/12	12/05/12	199d	E&M0320	E&M0670, E&M0680								
E&M0350	Form 501 Submission to FSD (PS1 & PS2)	28	0	27/11/11	25/12/11	04/02/15	13/03/15	1103d	E&M2016									
Yung Shue Wan																		
Preliminary																		
YSW0020	Approval of Environmental Team	16	100	17/05/10 A	01/06/10 A	17/05/10 A	01/06/10 A		KD0020	YSW0030, YSW0040								
YSW0030	Baseline monitoring (Air & Noise)	14	100	31/07/10 A	22/08/10 A	31/07/10 A	22/08/10 A		YSW0020	YSW0035								
YSW0035	Baseline Monitoring Report Submission (A & N)	14	100	23/08/10 A	07/09/10 A	23/08/10 A	07/09/10 A		YSW0030	YSW0120, YSW0152, YSW0500,								
YSW0040	Baseline monitoring (Water)	213	100	30/07/10 A	31/12/10 A	30/07/10 A	31/12/10 A		YSW0020	YSW0350								
YSW0050	Erect Hoarding and Fencing	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A											
Section W1 - Slope Works in Portion A & C																		
YSW0075	Mobilization	30	100	17/05/10 A	15/06/10 A	17/05/10 A	15/06/10 A		KD0020	YSW0100								
YSW0080	Site Clearance	30	100	17/05/10 A	15/06/10 A	17/05/10 A	15/06/10 A			YSW0085, YSW0120								
YSW0085	Initial Survey	14	100	02/06/10 A	15/06/10 A	02/06/10 A	15/06/10 A		YSW0080	YSW0120								
YSW0090	Verify the Rock Boulder required Stabilization Wk	30	100	19/07/10 A	21/03/11 A	19/07/10 A	21/03/11 A			YSW0100, YSW0110								
YSW0100	Removal of Rock Boulder	280	100	20/09/10 A	03/06/11 A	20/09/10 A	03/06/11 A		YSW0075, YSW0090	YSW0150								
YSW0110	Stabilizing work for rock boulder	280	50	16/07/11 A	17/12/11	16/07/11 A	15/08/11	-124d	YSW0090	YSW0150								
YSW0120	Cut the slope to design profile	100	100	13/09/10 A	14/09/10 A	13/09/10 A	14/09/10 A		YSW0035, YSW0080, YSW0085	YSW0131, YSW0165								
YSW0131	Mobilization of Plant and Material of Soil Nails	20	100	01/09/10 A	14/09/10 A	01/09/10 A	14/09/10 A		YSW0120	YSW0132								
YSW0132	Erect Scaffold and Working Platform	20	100	15/09/10 A	16/09/10 A	15/09/10 A	16/09/10 A		YSW0131	YSW0133								
YSW0133	Setting out and Verify Locations of Soil Nails	10	100	14/09/10 A	31/10/10 A	14/09/10 A	31/10/10 A		YSW0132	YSW0134								
YSW0134	Drilling and Soil Nails Installation	20	100	08/10/10 A	19/11/10 A	08/10/10 A	19/11/10 A		YSW0133	YSW0135								
YSW0135	Construction of Nail Heads	10	100	24/11/10 A	01/12/10 A	24/11/10 A	01/12/10 A		YSW0134	YSW0136								
YSW0136	Mesh Installation on Cut Slope	10	100	04/12/10 A	04/12/10 A	04/12/10 A	04/12/10 A		YSW0135	YSW0137								
YSW0137	Hydroseeding	30	0	31/07/11	29/08/11	27/06/11	27/07/11	-33d	YSW0136	YSW0140								
YSW0140	Construct U-channels & Step Channel on Cut Slope	116	90	02/04/11 A	10/09/11	02/04/11 A	08/08/11	-33d	YSW0137	YSW0150								
YSW0150	Construction of access, u-channels and catch pit	76	90	10/01/11 A	17/12/11	10/01/11 A	15/08/11	-124d	YSW0100, YSW0110, YSW0140,	KD0030								
YSW0165	Construction of Barrier Wall (below Ground Lev)	226	92	10/09/10 A	18/08/11	10/09/10 A	08/08/11	-10d	YSW0120	YSW0150, YSW0154, YSW0155								
Section W2 - YSW STW & Submarine Outfall																		
Civil & Structural Work																		
YSW0412	Mobilization	30	100	17/05/10 A	15/06/10 A	17/05/10 A	15/06/10 A		KD0020	YSW0422								
YSW0422	Site Clearance	30	100	17/05/10 A	15/06/10 A	17/05/10 A	15/06/10 A		KD0020, YSW0412	YSW0432, YSW0500, YSW0610,								
YSW0432	Initial Survey	14	100	02/06/10 A	15/06/10 A	02/06/10 A	15/06/10 A		YSW0422	YSW0510								
YSW STP - GL H - T																		
YSW0500	ELS & Excavation for Inlet Pumping Station	62	100	17/09/10 A	16/12/10 A	17/09/10 A	16/12/10 A		YSW0035, YSW0422	YSW0510								
YSW0510	Sub-structure construction (Inlet Pumping Stn)	30	100	17/12/10 A	04/04/11 A	17/12/10 A	04/04/11 A		YSW0432, YSW0500	YSW0520								
YSW0520	Backfill & Remove ELS (Inlet Pumping Stn)	30	100	03/01/11 A	05/05/11 A	03/01/11 A	05/05/11 A		YSW0510	YSW0530, YSW0610								
YSW0530	ELS & Excavation for Equalization Tank	40	100	11/01/11 A	08/06/11 A	11/01/11 A	08/06/11 A		YSW0520	YSW0540								
YSW0540	Sub-structure construction (Equalization Tank)	40	85	13/06/11 A	05/08/11	13/06/11 A	13/02/11	-173d	YSW0530	YSW0550								
YSW0550	Backfilling & Remove ELS (Equalization Tank)	40	0	06/08/11	14/09/11	14/02/11	25/03/11	-173d	YSW0540	YSW0570								
YSW0570	Excavate to formation by open cut	30	80	02/07/11 A	20/09/11	02/07/11 A	31/03/11	-173d	YSW0550	YSW0580								
YSW0580	Base slab construction	30	10	06/07/11 A	17/10/11	06/07/11 A	27/04/11	-173d	YSW0570	YSW0590								
YSW0590	G/F to 1/F construction	50	0	18/10/11	06/12/11	28/04/11	16/06/11	-173d	YSW0580	YSW0600								
YSW STP - GL T - X																		
YSW0610	Excavate to formation	50	100	08/09/10 A	17/09/10 A	08/09/10 A	17/09/10 A		YSW0035, YSW0422, YSW0520	YSW0620								
YSW0620	Base slab construction	60	100	18/09/10 A	23/05/11 A	18/09/10 A	23/05/11 A		YSW0610	YSW0630								
YSW0630	G/F to 1/F construction	95	100	27/12/10 A	19/07/11 A	27/12/10 A	19/07/11 A		YSW0620	YSW0640								
YSW0640	1/F to Roof Construction	91	10	20/07/11 A	20/10/11	20/07/11 A	21/08/11	-60d	YSW0630	YSW0810, YSW0840								
YSW0810	ABWF Installation	86	0	30/08/11	24/11/11	02/07/11	25/09/11	-60d	YSW0640	E&M0610, E&M0620, E&M0630,								
YSW STP - GL F - H & DN Tanks																		
YSW0650	ELS & Excavation for DN Tanks	70	100	21/08/10 A	14/10/10 A	21/08/10 A	14/10/10 A		YSW0035, YSW0422	YSW0660								
YSW0660	Sub-structure construction (DN Tanks)	40	100	15/10/10 A	31/12/10 A	15/10/10 A	31/12/10 A		YSW0650	YSW0670								
YSW0670	Backfill & Remove ELS (DN Tanks)	32	100	08/01/11 A	15/03/11 A	08/01/11 A	15/03/11 A		YSW0660	YSW0680								
YSW0680	Base slab construction	30	100	16/03/11 A	28/03/11 A	16/03/11 A	28/03/11 A		YSW0670	YSW0690								

Start date 05/05/10
 Finish date 13/03/15
 Data date 31/07/11
 Run date 08/08/11
 Page number 2A

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Progress point
- Critical point
- Summary point
- Start milestone point
- Finish milestone point

Leader Civil Engineering Corp. Ltd.
 Contract No. DC/2009/13
 Construction of Sewage Treatment Works at YSW & SKW
 3-month Rolling Programme (Aug 2011 - Oct 2011)

Date	Revision	Checked	Approved
31/07/10	Revision 0	StL	VC

(Marked on 31 Jul 2011)

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2011						
											MAY	JUN	JUL	AUG	SEP	OCT	NOV
YSW0690	Superstructure construction upto +10.5mPD	60	100	30/03/11 A	18/06/11 A	30/03/11 A	18/06/11 A		YSW0690	YSW0700, YSW0820							
YSW0700	Apply protective paint	20	0	31/07/11	19/08/11	27/02/11	18/03/11	-154d	YSW0690	YSW0710							
YSW0710	Water test	14	0	20/08/11	02/09/11	19/03/11	01/04/11	-154d	YSW0700	E&M0510, E&M0630, E&M0640							
YSW0820	ABWF installation	34	0	31/07/11	02/09/11	27/02/11	01/04/11	-154d	YSW0690	E&M0510, E&M0630, E&M0640							
YSW STP - GL A - F																	
YSW0730	Completion of HDD	0	0	20/10/11		01/07/11		-112d	YSW0360	YSW0740							
YSW0740	ELS & excavate for Outfall Shaft	22	0	20/10/11	11/11/11	01/07/11	22/07/11	-112d	YSW0730	YSW0750							
YSW0750	Sub-structure construction (outfall shaft)	22	0	11/11/11	03/12/11	23/07/11	13/08/11	-112d	YSW0740	YSW0760							
YSW0760	Backfill & remove ELS (outfall shaft)	24	0	03/12/11	27/12/11	14/08/11	06/09/11	-112d	YSW0750	YSW0770, YSW1470							
Fire Hose Reel / Sprinkler Pump Rm																	
YSW0840	ELS & excavate to formation (+0 mPD approx.)	30	0	20/10/11	19/11/11	01/09/11	30/09/11	-50d	YSW0035, YSW0422, YSW0640	YSW0860							
YSW0860	Sub-structure construction	30	0	19/11/11	19/12/11	01/10/11	30/10/11	-50d	YSW0840	YSW0880							
Road, Drain, Cable Draw Pits & Ducting																	
YSW0152	Temporary Diversion of Drainage	92	100	02/12/10 A	09/05/11 A	02/12/10 A	09/05/11 A		YSW0035	YSW0153							
YSW0153	Removal of Ex U-Channel where clash with B. Wall	50	100	20/11/10 A	20/04/11 A	20/11/10 A	20/04/11 A		YSW0152	YSW0154							
YSW0154	Construction of Subsoil Drain	90	0	18/08/11	16/11/11	08/10/11	05/01/12	51d	YSW0153, YSW0165	YSW0155							
YSW0155	RC Concrete Barrier (above Ground Level)	120	0	16/11/11	15/03/12	06/01/12	04/05/12	51d	YSW0154, YSW0165	YSW1640, YSW1660							
Submarine Outfall																	
YSW0180	Coordination of HEC	53	100	17/05/10 A	08/07/10 A	17/05/10 A	08/07/10 A			YSW0350							
YSW0200	Submission and Approval of Ecologist	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A			YSW0210							
YSW0210	Ecology Survey	90	100	16/07/10 A	11/02/11 A	16/07/10 A	11/02/11 A		YSW0200	YSW0350							
YSW0220	Submission and Approval of In. Hydro Survey	90	100	17/05/10 A	27/08/10 A	17/05/10 A	27/08/10 A			YSW0230							
YSW0230	Hydrographical Survey (YSW)	45	100	31/08/10 A	31/01/11 A	31/08/10 A	31/01/11 A		YSW0220	YSW0350							
YSW0240	Material Submission, Approval of HDPE pipe	93	100	17/05/10 A	31/03/11 A	17/05/10 A	31/03/11 A			YSW0250							
YSW0250	Submit and Approval of Method Statement for HDD	120	100	24/09/10 A	25/03/11 A	24/09/10 A	25/03/11 A		YSW0240	YSW0260, YSW0270, YSW0340							
YSW0260	Submission of HDD Method Statement to HEC	14	100	26/01/11 A	24/03/11 A	26/01/11 A	24/03/11 A		YSW0250	YSW0320, YSW0340							
YSW0270	Additional G.I. Boreholes (YSW)	62	100	06/11/10 A	19/01/11 A	06/11/10 A	19/01/11 A		YSW0250	YSW0280, YSW0320							
YSW0280	Submission of propose alignment to the Eng	14	100	02/02/11 A	04/03/11 A	02/02/11 A	04/03/11 A		YSW0270	YSW0290, YSW0310, YSW0340							
YSW0290	Submission of Marine Notice	60	100	31/01/11 A	29/03/11 A	31/01/11 A	29/03/11 A		YSW0280	YSW0350							
YSW0310	Construction of Entry Pit and Preparation Work	39	100	15/03/11 A	31/03/11 A	15/03/11 A	31/03/11 A		YSW0280	YSW0320, YSW0330							
YSW0320	Prepare of HDD Drill Rig Set-up (YSW)	39	100	02/04/11 A	28/04/11 A	02/04/11 A	28/04/11 A		YSW0260, YSW0270, YSW0310	YSW0330, YSW0350							
YSW0330	Establishment of HDD plant & equipment	14	100	09/04/11 A	14/04/11 A	09/04/11 A	14/04/11 A		YSW0310, YSW0320	YSW0340							
YSW0340	Setting up at drillhole location	7	100	19/04/11 A	28/04/11 A	19/04/11 A	28/04/11 A		YSW0250, YSW0260, YSW0280,	YSW0350							
YSW0350	Drill pilot hole and reaming hole - NS400 - 530m	123	45	29/04/11 A	06/10/11	29/04/11 A	16/06/11	-112d	YSW0040, YSW0180, YSW0210,	YSW0360							
YSW0360	Installation of NS400 HDPE 530m	14	0	06/10/11	20/10/11	17/06/11	30/06/11	-112d	YSW0350	SKW1181, YSW0365, YSW0370,							
YSW0365	Set up of Silt Curtain as per EP	30	0	20/10/11	19/11/11	20/07/13	18/08/13	638d	YSW0360	YSW0370							
YSW0370	Dredging of Marine Deposit for Diffuser (YSW)	60	0	19/11/11	18/01/12	19/08/13	17/10/13	638d	YSW0360, YSW0365	YSW0380							
E&M Works - YSW STP																	
E&M0360	Delivery of MBR Memb. Mod. (MBR Tk4)	137	100	18/06/11 A	21/06/11 A	18/06/11 A	21/06/11 A		E&M0160	E&M0510							
E&M0370	Delivery of MBR Membrane Modules - 2nd Shipment	150	0	31/07/11	27/12/11	29/09/11	25/02/12	60d	E&M0160	E&M0520							
E&M0380	Delivery of Grit Removal Equipment	180	0	18/09/11	16/03/12	29/05/11	24/11/11	-113d	E&M0150	E&M0530							
E&M0390	Delivery of Coarse Screens	162	0	19/08/11	28/01/12	02/04/11	10/09/11	-140d	E&M0110	E&M0540							
E&M0400	Delivery of Fine Screens	180	0	18/09/11	16/03/12	29/05/11	24/11/11	-113d	E&M0120	E&M0550							
E&M0410	Delivery of Pumps	162	0	18/09/11	27/02/12	02/04/11	10/09/11	-170d	E&M0130	E&M0560							
E&M0420	Delivery of Submersible Mixers	162	0	19/08/11	28/01/12	01/07/11	09/12/11	-50d	E&M0140	E&M0570							
E&M0440	Delivery of Sludge Dewatering Equipment	180	0	18/09/11	16/03/12	02/04/11	28/09/11	-170d	E&M0170	E&M0580							
E&M0450	Delivery of Valves, Pipes & Fittings	180	0	18/09/11	16/03/12	28/07/11	23/01/12	-53d	E&M0180	E&M0590, E&M0605							
E&M0460	Delivery of Penstocks	180	0	18/09/11	16/03/12	11/07/11	06/01/12	-70d	E&M0190	E&M0600							
E&M0470	Delivery of Instruments	180	0	18/09/11	16/03/12	08/11/11	05/05/12	51d	E&M0200	E&M0610							
E&M0480	Delivery of MCC LVSB	177	0	18/09/11	13/03/12	02/04/11	25/09/11	-170d	E&M0210	E&M0620							
E&M0490	Delivery of BS Equipment	180	0	29/09/11	26/03/12	30/08/11	25/02/12	-30d	E&M0220	E&M0630							
E&M0500	Delivery FS Equipment	180	0	29/09/11	26/03/12	27/09/11	24/03/12	-2d	E&M0230	E&M0330, E&M0640							
E&M0510	Install Membrane Modules in MBR Tank no. 4	90	0	03/09/11	01/12/11	02/04/11	30/06/11	-154d	E&M0360, YSW0710, YSW0820	KD0115							

Sok Kwu Wan

Preliminary

Start date 05/05/10
 Finish date 13/03/15
 Data date 31/07/11
 Run date 08/08/11
 Page number 3A

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ▲ Progress point
- ▼ Critical point
- ◆ Summary point
- ◆ Start milestone point
- ◆ Finish milestone point

© Primavera Systems, Inc.

Leader Civil Engineering Corp. Ltd.
 Contract No. DC/2009/13
 Construction of Sewage Treatment Works at YSW & SKW
 3-month Rolling Programme (Aug 2011 - Oct 2011)

(Marked on 31 Jul 2011)

Date	Revision	Checked	Approved
31/07/10	Revision 0	STL	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2011							
											MAY	JUN	JUL	AUG	SEP	OCT	NOV	
SKW0250	Approval of Environmental Team	16	100	17/05/10 A	01/06/10 A	17/05/10 A	01/06/10 A		KD0020	SKW0260								
SKW0260	Baseline monitoring (Air & Noise)	14	100	02/06/10 A	15/06/10 A	02/06/10 A	15/06/10 A		SKW0250	SKW0242, SKW0265, SKW0592,								
SKW0265	Baseline Monitoring Submission (A & N)	14	100	16/06/10 A	08/07/10 A	16/06/10 A	08/07/10 A		SKW0260	SKW0242, SKW0592, SKW0681,								
Section W3 - Footpath Diversion in Portion G																		
Civil & Geotechnical Works																		
SKW0240	Site Clearance	21	100	17/05/10 A	06/06/10 A	17/05/10 A	06/06/10 A			SKW0241								
SKW0241	Initial Survey	9	100	07/06/10 A	15/06/10 A	07/06/10 A	15/06/10 A		SKW0240	SKW0242								
SKW0242	Excavation to formation for Bay 1 to 5	50	100	16/06/10 A	11/08/10 A	16/06/10 A	11/08/10 A		SKW0241, SKW0260, SKW0265	SKW0251								
SKW0251	Drill & Install Dowel Bar for Bay 1 & 3	20	100	02/08/10 A	01/09/10 A	02/08/10 A	01/09/10 A		SKW0242	SKW0301								
SKW0301	Erect Formwork, mesh & weephole for Bay 1 & 3	12	100	02/09/10 A	15/09/10 A	02/09/10 A	15/09/10 A		SKW0251	SKW0311								
SKW0311	Concreting for Bay 1 & 3	12	100	19/06/10 A	29/09/10 A	19/06/10 A	29/09/10 A		SKW0301	SKW0321								
SKW0321	Drilling & install Dowel Bar for Bay 2 & 5	6	100	30/09/10 A	06/10/10 A	30/09/10 A	06/10/10 A		SKW0311	SKW0331								
SKW0331	Erect Formwork, mesh & weephole for Bay 2 & 5	7	100	07/10/10 A	13/10/10 A	07/10/10 A	13/10/10 A		SKW0321	SKW0341								
SKW0341	Concreting for Bay 2 & 5	7	100	14/10/10 A	20/10/10 A	14/10/10 A	20/10/10 A		SKW0331	SKW0351								
SKW0351	Excavation to formation for Bay 6 to 9	20	100	21/10/10 A	10/11/10 A	21/10/10 A	10/11/10 A		SKW0341	SKW0361								
SKW0361	Drill & install dowel Bar for Bay 4 & 7	6	100	11/11/10 A	16/11/10 A	11/11/10 A	16/11/10 A		SKW0351	SKW0371								
SKW0371	Erect formwork, mesh & weephole for Bay 4 & 7	7	100	11/11/10 A	16/11/10 A	11/11/10 A	16/11/10 A		SKW0361	SKW0381								
SKW0381	Concreting for Bay 4 & 7	7	100	17/11/10 A	23/11/10 A	17/11/10 A	23/11/10 A		SKW0371	SKW0391								
SKW0391	Drill & install dowel Bar for Bay 6 & 9	3	100	24/11/10 A	27/11/10 A	24/11/10 A	27/11/10 A		SKW0381	SKW0401								
SKW0401	Erect formwork, mesh & weephole for Bay 6 & 9	7	100	28/11/10 A	05/12/10 A	28/11/10 A	05/12/10 A		SKW0391	SKW0411								
SKW0411	Concreting for Bay 6 & 9	7	100	06/12/10 A	12/12/10 A	06/12/10 A	12/12/10 A		SKW0401	SKW0421								
SKW0421	Drill & install dowel Bar for Bay 8	1	100	13/12/10 A	13/12/10 A	13/12/10 A	13/12/10 A		SKW0411	SKW0431								
SKW0431	Erect formwork, mesh & weephole for Bay 8	4	100	15/12/10 A	21/12/10 A	15/12/10 A	21/12/10 A		SKW0421	SKW0441								
SKW0441	Concreting for Bay 8	4	100	22/12/10 A	27/12/10 A	22/12/10 A	27/12/10 A		SKW0431	SKW0461								
SKW0461	Excavation for no fine concrete Bay (1-9)	3	100	26/07/11 A	28/07/11 A	26/07/11 A	28/07/11 A		SKW0441	SKW0471								
SKW0471	Concreting for no-fine concrete	7	100	01/02/11 A	07/02/11 A	01/02/11 A	07/02/11 A		SKW0461	SKW0481								
SKW0481	Installation of Wall tie & stone facing	14	100	08/02/11 A	11/02/11 A	08/02/11 A	11/02/11 A		SKW0471	SKW0491								
SKW0491	Construction of Gabion Wall	7	100	08/02/11 A	14/02/11 A	08/02/11 A	14/02/11 A		SKW0481	SKW0501								
SKW0501	Place Geotextile	3	100	08/01/11 A	28/02/11 A	08/01/11 A	28/02/11 A		SKW0491	SKW0511								
SKW0511	Backfill behind the retaining wall to approx. +4	7	100	11/01/11 A	28/02/11 A	11/01/11 A	28/02/11 A		SKW0501	SKW0521								
SKW0521	Watermain Laying and Diversion	14	100	01/04/11 A	10/05/11 A	01/04/11 A	10/05/11 A		SKW0511	SKW0531								
SKW0531	Concreting for Pavement	7	100	02/06/11 A	30/07/11 A	02/06/11 A	30/07/11 A		SKW0521	SKW0541								
SKW0541	Installation of Flower Pot	7	0	31/07/11	06/08/11	15/02/11	22/02/11	-166d	SKW0531	SKW0551								
SKW0551	Permanent Footpath Diversion	1	100	30/07/11 A	30/07/11 A	30/07/11 A	30/07/11 A		SKW0541	KD0050, SKW1261, SKW1311								
Section W4 - Slope Works in Portions H & I																		
Geotechnical Works																		
SKW0588	Construct scaffolding access	30	100	15/06/10 A	14/07/10 A	15/06/10 A	14/07/10 A		KD0020	SKW0590								
SKW0590	Site Clearance for Slope	100	100	15/07/10 A	22/10/10 A	15/07/10 A	22/10/10 A		SKW0588	SKW0591								
SKW0591	Initial Survey for Slope	28	100	21/09/10 A	18/10/10 A	21/09/10 A	18/10/10 A		SKW0590	SKW0592								
SKW0592	Temporary Rockfall fence at ex. Footpath	43	100	19/10/10 A	06/01/11 A	19/10/10 A	06/01/11 A		SKW0260, SKW0265, SKW0591	SKW05931								
SKW05931	Construction of Haul Road (To +21mPD)	50	100	28/11/10 A	30/12/10 A	28/11/10 A	30/12/10 A		SKW0592	SKW05932								
SKW05932	Construction of Haul Road (To +42mPD)	60	100	15/12/10 A	31/01/11 A	15/12/10 A	31/01/11 A		SKW05931	SKW05933, SKW05940, SKW0595								
SKW05933	Excavation of Rock Berm (+50mPD to +42.5mPD)	30	100	01/03/11 A	03/05/11 A	01/03/11 A	03/05/11 A		SKW05932	SKW05934								
SKW05934	Excavation of Rock Berm (+42.5mPD to +35mPD)	30	100	04/05/11 A	31/05/11 A	04/05/11 A	31/05/11 A		SKW05933	SKW05935, SKW05941								
SKW05935	Excavation of Rock Berm (+35mPD to +27.5mPD)	30	20	02/07/11 A	23/08/11	02/07/11 A	21/03/11	-155d	SKW05934	SKW05936								
SKW05936	Excavation of Rock Berm (+27.5mPD to +20mPD)	30	0	24/08/11	22/09/11	22/03/11	20/04/11	-155d	SKW05935	SKW05937, SKW05942								
SKW05937	Excavation of Rock Berm (+20mPD to +12.5mPD)	30	0	23/09/11	22/10/11	21/04/11	20/05/11	-155d	SKW05936	SKW05938								
SKW05938	Excavation of Rock Berm (+12.5mPD to +5mPD)	28	0	23/10/11	19/11/11	21/05/11	17/06/11	-155d	SKW05937	SKW05943, SKW1311, SKW1371								
SKW05940	Slope Drainage & Misc. at 50mPD	60	100	01/04/11 A	03/05/11 A	01/04/11 A	03/05/11 A		SKW05932	SKW05941								
SKW05941	Slope Drainage & Misc. (+50 to +35mPD)	60	40	04/05/11 A	04/09/11	04/05/11 A	20/04/11	-137d	SKW05934, SKW05940	SKW05942								
SKW05942	Slope Drainage & Misc. (+35 to +20mPD)	58	0	23/09/11	19/11/11	21/04/11	17/06/11	-155d	SKW05936, SKW05941	SKW05943								
SKW0595	Rock Meshing & Rockfall Fence	260	0	31/07/11	15/04/12	29/11/10	15/08/11	-244d	SKW05932	KD0060								
Section W5 - P.S. No. 1 in Portion D																		
Civil & Geotechnical Works																		
SKW0651	Site Clearance	7	100	17/05/10 A	23/05/10 A	17/05/10 A	23/05/10 A		KD0020	SKW0652								
SKW0652	Initial Survey	7	100	24/05/10 A	30/05/10 A	24/05/10 A	30/05/10 A		SKW0651	SKW0661, SKW0681								

Start date	05/05/10	Early bar
Finish date	13/03/15	Progress bar
Data date	31/07/11	Critical bar
Run date	08/08/11	Summary bar
Page number	4A	Progress point
		Critical point
		Summary point
		Start milestone point
		Finish milestone point

Leader Civil Engineering Corp. Ltd.
 Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
 3-month Rolling Programme (Aug 2011 - Oct 2011)

Date	Revision	Checked	Approved
31/07/10	Revision 0	STL	VC

(Marked on 31 Jul 2011)

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2011										
											MAY	JUN	JUL	AUG	SEP	OCT	NOV				
E&M2016	Delivery of FS Equipment	107	0	12/08/11	27/11/11	15/01/11	01/05/11	-209d	E&M2006	E&M0350, E&M2106											
E&M2017	Delivery of BS Equipment	107	0	12/08/11	27/11/11	15/01/11	01/05/11	-209d	E&M2007	E&M2107											
Installation, T&C																					
E&M2105	Install Instrumentation	55	0	04/12/11	28/01/12	02/05/11	25/06/11	-216d	E&M2015, SKW1051, SKW1061	E&M2140											
E&M2106	Install FS Equipment	55	0	04/12/11	28/01/12	02/05/11	25/06/11	-216d	E&M2016, SKW1051, SKW1061	E&M2140											
E&M2107	Install BS Equipment	55	0	04/12/11	28/01/12	02/05/11	25/06/11	-216d	E&M2017, SKW1051, SKW1061	E&M2110, E&M2140											
Section W7 - SKW STW, Sewer and Submarine Outfall																					
Submarine Outfall																					
SKW1130	Approval of IHS Consultant	180	100	17/05/10 A	27/08/10 A	17/05/10 A	27/08/10 A			SKW1131											
SKW1131	Hydrographical Survey (SKW)	300	100	01/02/11 A	28/02/11 A	01/02/11 A	28/02/11 A		KD0020, SKW1130	SKW1231											
SKW1141	Baseline Monitoring (Water)	213	100	27/07/10 A	31/12/10 A	27/07/10 A	31/12/10 A		SKW0260, SKW0265	SKW1151											
SKW1151	Set up Temporary Working Platform	185	80	15/06/11 A	05/09/11	15/06/11 A	15/09/11	10d	PRE0090, SKW1141	SKW1171											
SKW STW																					
Submission & Delivery (E&M)																					
E&M3010	Delivery of MBR M.M. - 1st shipment for Temp STP	150	0	31/07/11	27/12/11	10/03/14	20/08/14	953d	E&M0160	E&M3170											
E&M3030	Delivery of Grit Removal Equipment	180	0	18/09/11	16/03/12	31/08/11	26/02/12	-19d	E&M0150	E&M3190											
E&M3060	Delivery of Fine Screens	136	0	18/09/11	01/02/12	15/08/11	28/12/11	-35d	E&M0120	E&M3210											
E&M3070	Delivery of Pumps	136	0	18/09/11	01/02/12	15/08/11	28/12/11	-35d	E&M0130	E&M3220											
E&M3080	Delivery of Submersible Mixers	180	0	19/08/11	15/02/12	15/09/11	12/03/12	27d	E&M0140	E&M3230											
E&M3090	Delivery of Sludge Dewatering Equipment	210	0	18/09/11	15/04/12	18/07/11	12/02/12	-63d	E&M0170	E&M3240											
E&M3100	Delivery of Valves, Pipes & Fittings	180	0	18/09/11	16/03/12	22/12/13	19/06/14	826d	E&M0180	E&M3250											
E&M3110	Delivery of Penstocks	180	0	18/09/11	16/03/12	04/01/14	02/07/14	839d	E&M0190	E&M3260											
E&M3130	Delivery of Instruments	180	0	18/09/11	16/03/12	20/03/14	15/10/14	914d	E&M0200	E&M3270											
E&M3140	Delivery of MCC LVSB	180	0	18/09/11	16/03/12	09/05/11	04/11/11	-133d	E&M0210	E&M3261											
E&M3150	Delivery of BS Equipment	180	0	29/09/11	26/03/12	06/01/14	04/07/14	830d	E&M0220	E&M3291											
E&M3160	Delivery of FS Equipment	180	0	29/09/11	26/03/12	14/01/12	11/07/12	107d	E&M0230	E&M0340, E&M3300											
Construction of Grid A-G																					
SKW1261	Excavate for SKW STW Structure (Grid A -G)	164	5	30/07/11 A	09/01/12	30/07/11 A	27/07/11	-166d	SKW0551	SKW1271, SKW1371											
Construction of Grid G-N																					
SKW1311	Excavate for SKW STW Structure (Grid G-N)	36	0	20/11/11	25/12/11	29/06/11	03/08/11	-144d	SKW0551, SKW0598	SKW1321											
Rising Main																					
SKW1481	Subm, Approval & Delivery of DI pipes	120	100	17/05/10 A	28/02/11 A	17/05/10 A	28/02/11 A		KD0020	SKW1501											
SKW1501	Concrete Trough (ChB0+00 - ChB1+20)	300	0	31/07/11	25/05/12	14/09/10	10/07/11	-320d	PRE0100, SKW1481	SKW1521											
Section W8 - Landscape Softworks in All Portions																					
SKW1591	Tree Survey	21	100	17/05/10 A	06/06/10 A	17/05/10 A	06/06/10 A		KD0020	SKW1621											
SKW1611	Preservation & Protection of Trees	822	55	17/05/10 A	03/08/12	17/05/10 A	03/08/12	0	KD0020	KD0100, SKW1631											
SKW1621	Transplantation at SKW	60	100	07/06/10 A	05/10/10 A	07/06/10 A	05/10/10 A		SKW1591												

Start date 05/05/10
 Finish date 13/03/15
 Data date 31/07/11
 Run date 08/08/11
 Page number 6A
 Primavera Systems, Inc.

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Progress point
- Critical point
- Summary point
- Start milestone point
- Finish milestone point










Leader Civil Engineering Corp. Ltd.
 Contract No. DC/2009/13
 Construction of Sewage Treatment Works at YSW & SKW
 3-month Rolling Programme (Aug 2011 - Oct 2011)

(Marked on 31 Jul 2011)

Date	Revision	Checked	Approved
31/07/10	Revision 0	StL	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2011							
											MAY	JUN	JUL	AUG	SEP	OCT	NOV	
+Project Key Date																		
		451	0	05/05/10 A	01/12/11	05/05/10 A	30/06/11	-154d										
+Preliminary (Civil)																		
		191	100	17/05/10 A	23/11/10 A	17/05/10 A	23/11/10 A		KD0020									
Preliminary (E&M)																		
Technical Submission																		
+Process Design of SKWSTW & YSWSTW																		
		457	92	17/05/10 A	16/08/11	17/05/10 A	30/06/11	-47d										
+Hydraulic Design																		
		448	95	17/05/10 A	07/08/11	17/05/10 A	30/06/11	-38d										
+Equipment Submission & Approval																		
		500	58	17/05/10 A	28/09/11	17/05/10 A	07/11/11	40d										
+Drawings Submission & Approval																		
		432	84	24/06/10 A	29/08/11	24/06/10 A	30/07/11	-30d										
+Statutory Submission																		
		189	0	29/09/11	04/04/12	01/07/11	13/03/15	1001d										
Yung Shue Wan																		
+Preliminary																		
		229	100	17/05/10 A	31/12/10 A	17/05/10 A	31/12/10 A											
+Section W 1 - Slope Works in Portion A & C																		
		580	84	17/05/10 A	17/12/11	17/05/10 A	15/08/11	-124d										
Section W 2 - YSW STW & Submarine Outfall																		
+Civil & Structural Work																		
		668	56	17/05/10 A	15/03/12	17/05/10 A	04/05/12	51d										
+Submarine Outfall																		
		612	83	17/05/10 A	18/01/12	17/05/10 A	17/10/13	638d										
+E&M Works - YSW STP																		
		283	6	18/06/11 A	26/03/12	02/04/11 A	05/05/12	40d										
Sok Kwu Wan																		
+Preliminary																		
		53	100	17/05/10 A	08/07/10 A	17/05/10 A	08/07/10 A											
Section W 3 - Footpath Diversion in Portion G																		
+Civil & Geotechnical Works																		
		447	98	17/05/10 A	06/08/11	17/05/10 A	30/07/11	-166d										
Section W 4 - Slope Works in Portions H & I																		
+Geotechnical Works																		
		671	50	15/06/10 A	15/04/12	15/06/10 A	15/08/11	-244d										
Section W 5 - P.S. No. 1 in Portion D																		
+Civil & Geotechnical Works																		
		319	100	17/05/10 A	31/03/11 A	17/05/10 A	31/03/11 A											
+Structural Works																		
		391	4	20/04/11 A	14/05/12	01/01/11 A	15/11/11	-181d										
Section W 6 - Sewer and PS No.2 in Portions E&H																		
+Civil & Geotechnical Works																		
		697	51	17/05/10 A	12/04/12	17/05/10 A	15/11/11	-149d										
+Structural Works																		
		431	1	02/05/11 A	06/07/12	18/12/10 A	15/11/11	-233d										
E&M Works (PS2)																		
+Submission & Delivery																		
		600	61	17/05/10 A	06/01/12	17/05/10 A	02/07/11	-188d										
+Installation, T&C																		
		55	0	04/12/11	28/01/12	02/05/11	25/06/11	-216d										
Section W 7 - SKW STW, Sewer and Submarine Outfall																		
+Submarine Outfall																		
		477	96	17/05/10 A	05/09/11	17/05/10 A	15/09/11	10d										

Start date	05/05/10
Finish date	13/03/15
Data date	31/07/11
Run date	08/08/11
Page number	1A
© Primavera Systems, Inc.	

-  Early bar
-  Progress bar
-  Critical bar
-  Summary bar
-  Progress point
-  Critical point
-  Summary point
-  Start milestone point
-  Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (Aug 2011 - Oct 2011)










(Outline page 1 of 2)

(Marked on 31 Jul 2011)

Date	Revision	Checked	Approved
31/07/10	Revision 0	StL	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2011						
											MAY	JUN	JUL	AUG	SEP	OCT	NOV
SKW STW																	
+Submission & Delivery (E&M)																	
		260	0	31/07/11	15/04/12	09/05/11	15/10/14	884d									
+Construction of Grid A-G																	
		164	5	30/07/11 A	09/01/12	30/07/11 A	27/07/11	-166d									
+Construction of Grid G-N																	
		36	0	20/11/11	25/12/11	29/06/11	03/08/11	-144d									
+Rising Main																	
		740	29	17/05/10 A	25/05/12	17/05/10 A	10/07/11	-320d									
+Section W 8 - Landscape Softworks in All Portions																	
		810	59	17/05/10 A	03/08/12	17/05/10 A	03/08/12	0									

Start date 05/05/10
 Finish date 13/03/15
 Data date 31/07/11
 Run date 08/08/11
 Page number 2A

-  Early bar
-  Progress bar
-  Critical bar
-  Summary bar
-  Progress point
-  Critical point
-  Summary point
-  Start milestone point
-  Finish milestone point

Leader Civil Engineering Corp. Ltd.
 Contract No. DC/2009/13
 Construction of Sewage Treatment Works at YSW & SKW
 3-month Rolling Programme (Aug 2011 - Oct 2011)


(Outline page 2 of 2)


(Marked on 31 Jul 2011)

Date	Revision	Checked	Approved
31/07/10	Revision 0	StL	VC


Appendix D

Location of Monitoring Stations (Air Quality / Construction Noise / Water Quality / Dive Surveys of Coral)

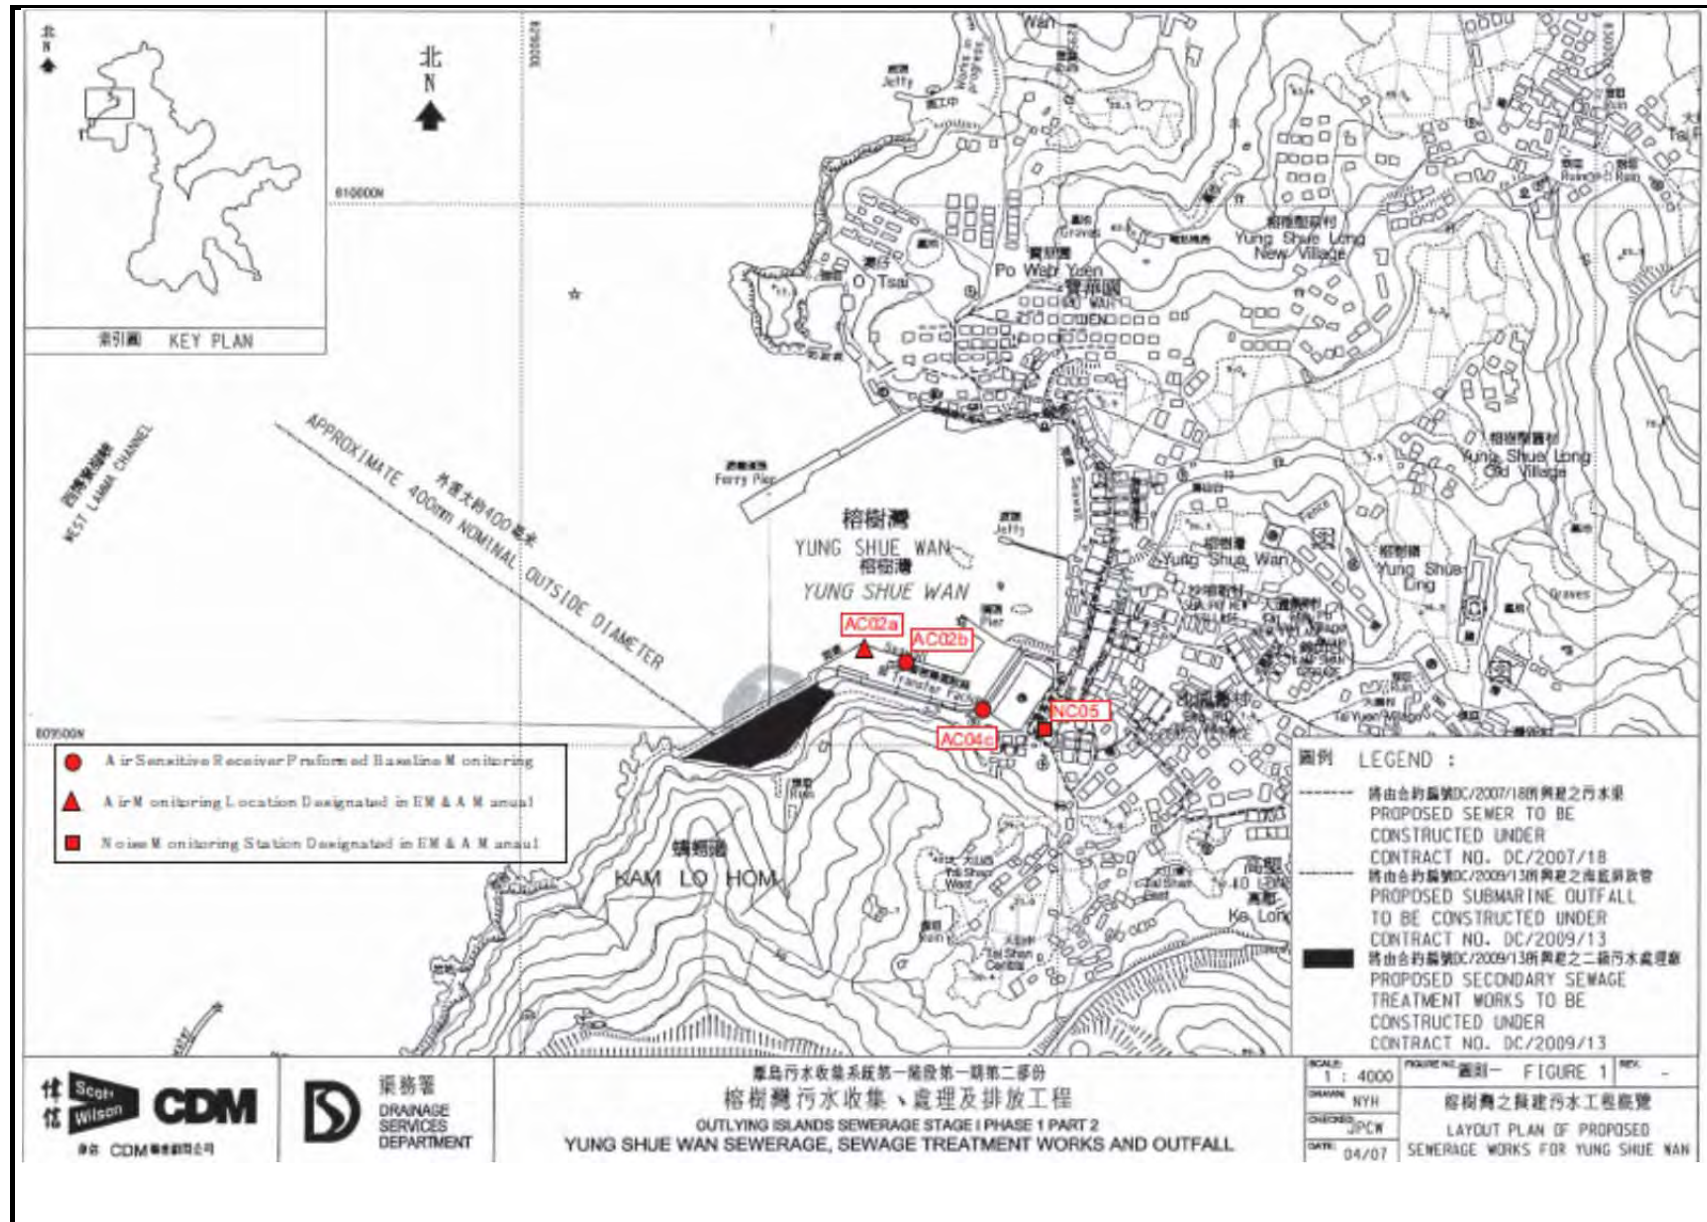


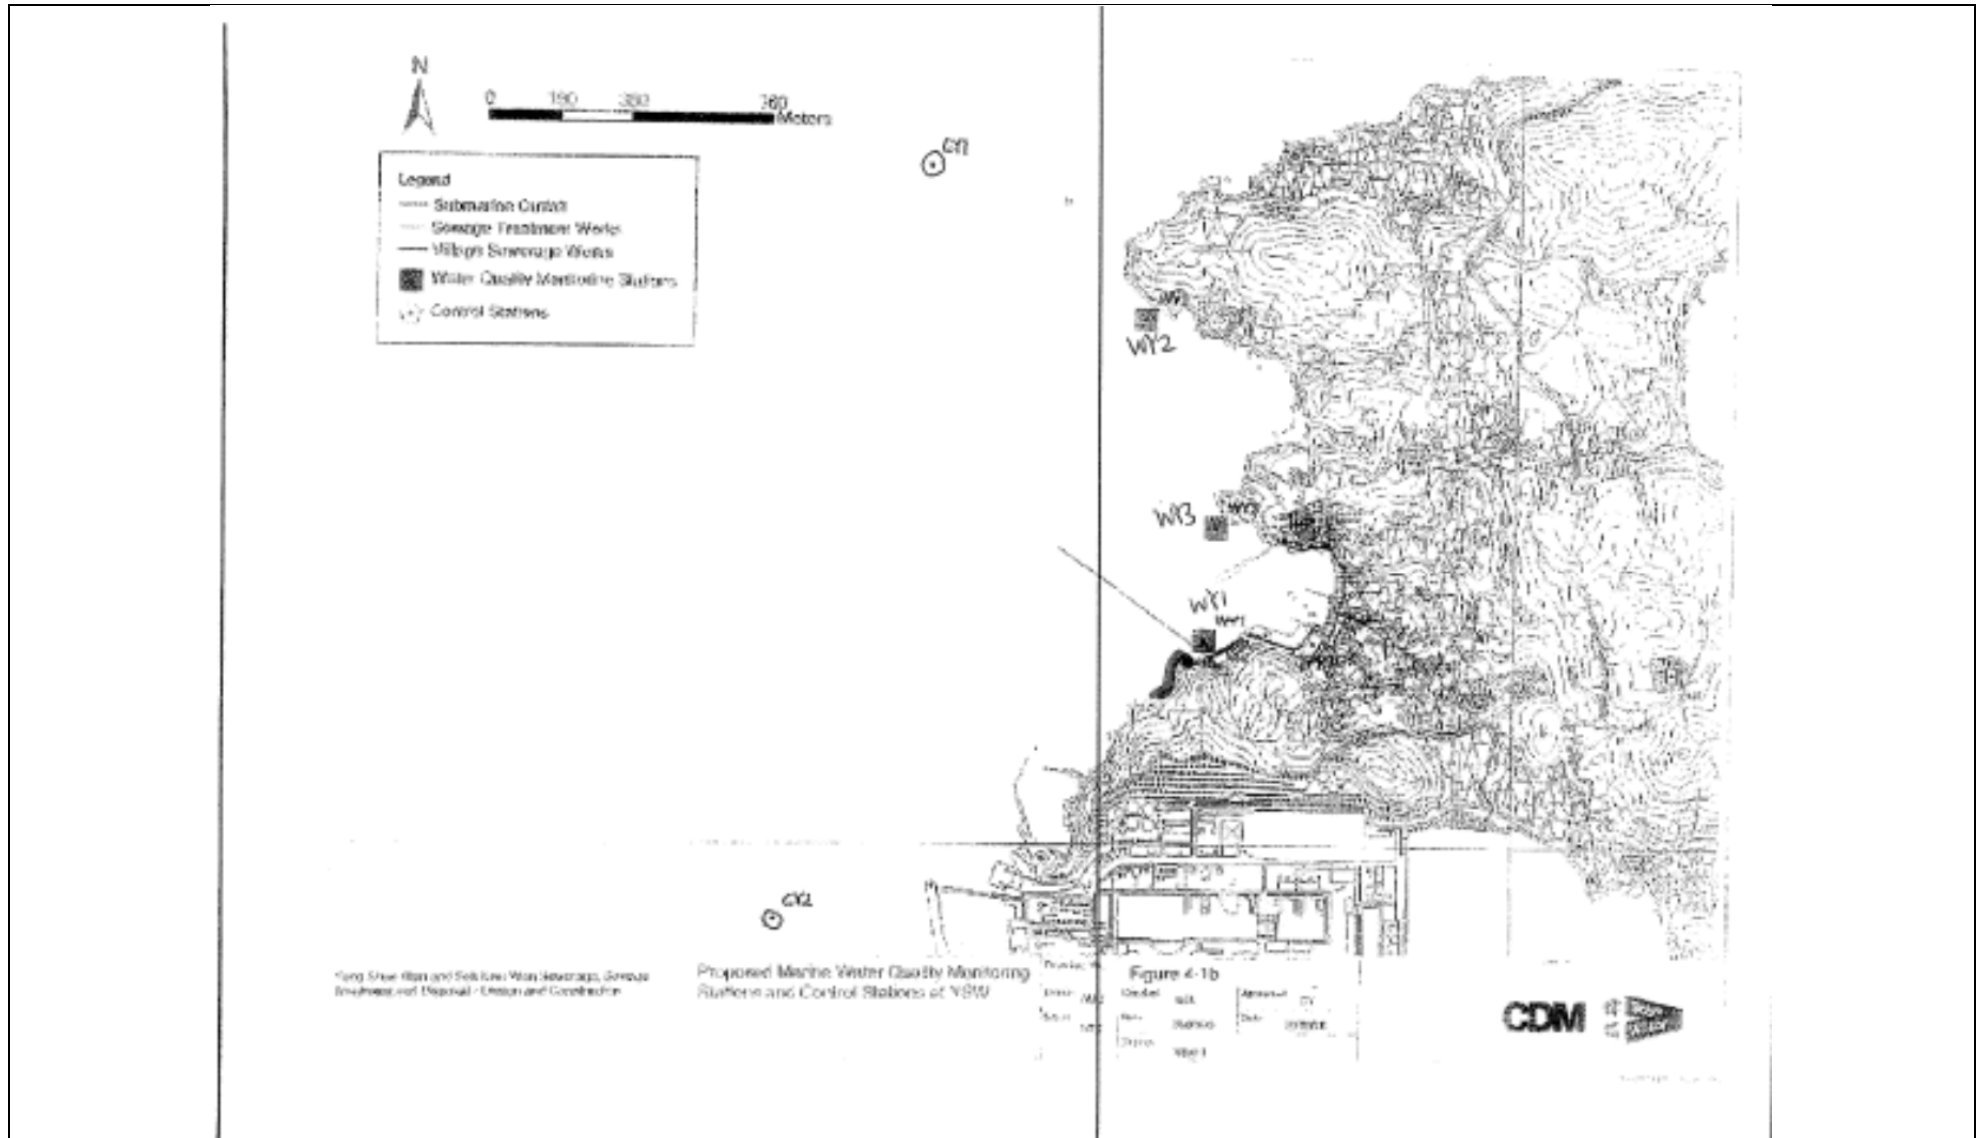

Coral Area at Yung Shue Wan Seawall

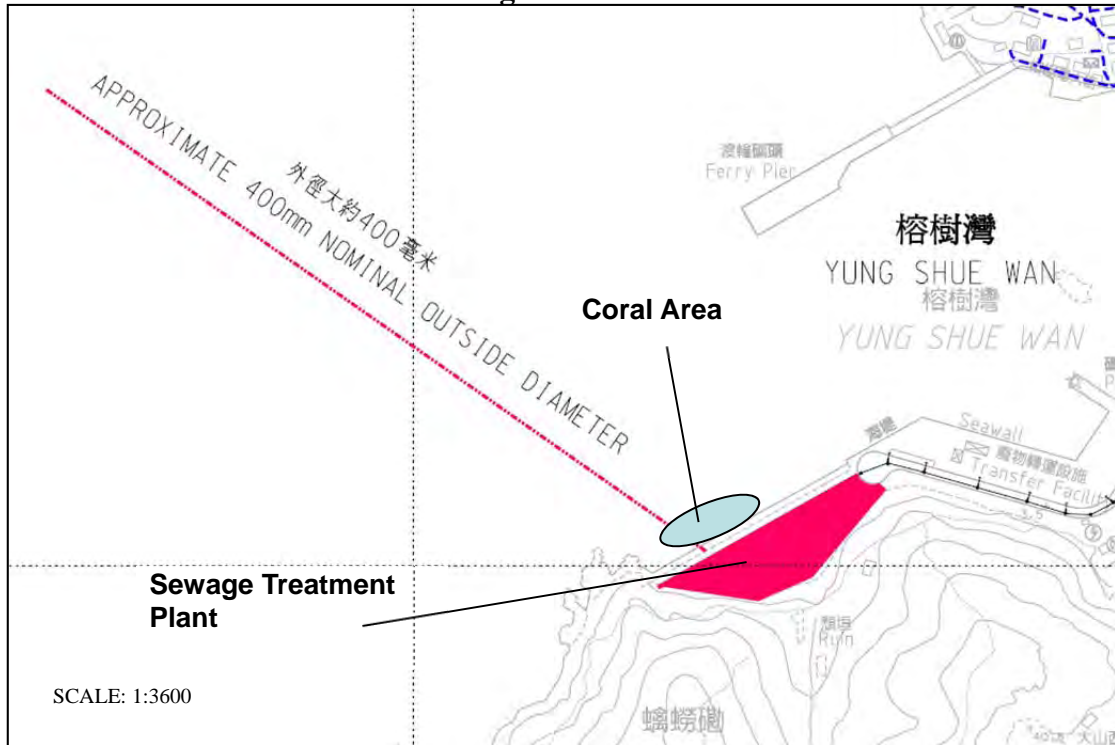

REA Transect at Yung Shue Wan Seawall

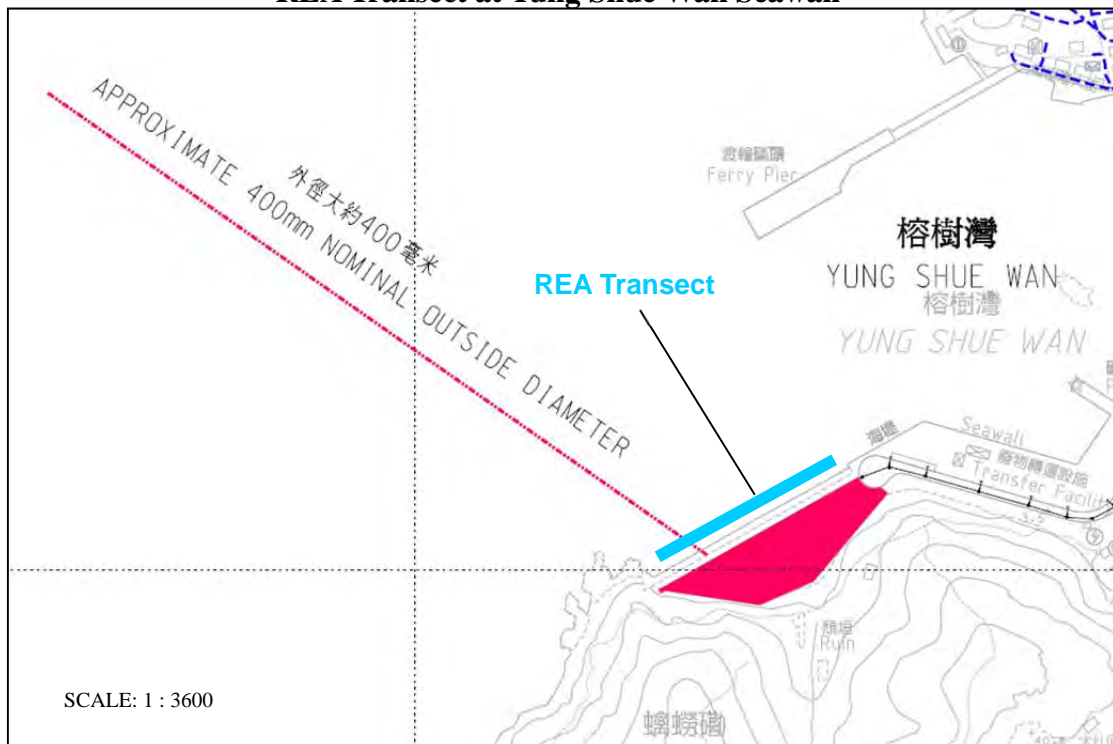

Coral Area at Sham Wan



REA Transect at Sham Wan



Appendix E

Monitoring Equipments Calibration Certificate



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE.
 VILLAGE OF CLEVELAND, OH 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Jun 02, 2011 Roots-meter S/N 0438320 Ta (K) - 294
 Operator Tisch Orifice I.D. - 1941 Pa (mm) - 754.38

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF. VOLUME (m3)	DIFF. TIME (min)	METER DIFF. Hg (mm)	ORIFICE DIFF. H2O (in.)
1	NA	NA	1.00	1.4660	3.3	2.00
2	NA	NA	1.00	1.0410	6.4	4.00
3	NA	NA	1.00	0.9310	8.1	5.00
4	NA	NA	1.00	0.8830	8.9	5.50
5	NA	NA	1.00	0.7310	13.0	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
1.0017	0.6833	1.4185	0.9956	0.6791	0.8829
0.9975	0.9582	2.0061	0.9914	0.9524	1.2486
0.9952	1.0690	2.2429	0.9892	1.0625	1.3959
0.9942	1.1260	2.3524	0.9882	1.1191	1.4641
0.9887	1.3526	2.8371	0.9827	1.3444	1.7657
Qstd slope (m) = 2.11693			Qa slope (m) = 1.32558		
intercept (b) = -0.02568			intercept (b) = -0.01598		
coefficient (r) = 0.99993			coefficient (r) = 0.99993		
y axis = SQRT[H2O(Pa/760)(298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

$$Vstd = \text{Diff. Vol} \left[\frac{(Pa - \text{Diff. Hg})}{760} \right] \left(\frac{298}{Ta} \right)$$

$$Qstd = Vstd / \text{Time}$$

$$Va = \text{Diff Vol} \left[\frac{(Pa - \text{Diff Hg})}{Pa} \right]$$

$$Qa = Va / \text{Time}$$

For subsequent flow rate calculations:

$$Qstd = 1/m \{ [\text{SQRT} (H2O (Pa/760) (298/Ta))] - b \}$$

$$Qa = 1/m \{ [\text{SQRT} H2O (Ta/Pa)] - b \}$$

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : YSW RE Offices
 Location ID : AC02b

Date of Calibration: 1-Aug-11
 Next Calibration Date: 1-Oct-11
 Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa)	1005.5	Corrected Pressure (mm Hg)	754.125
Temperature (°C)	29.5	Temperature (K)	303

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11693
Model->	5025A	Qstd Intercept ->	-0.02568
Serial # ->	1941		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.3	5.3	10.6	1.533	58	56.92	Slope = 30.4574 Intercept = 10.1094 Corr. coeff. = 0.9999
13	4.3	4.3	8.6	1.382	53	52.01	
10	3.3	3.3	6.6	1.212	48	47.10	
7	2.2	2.2	4.4	0.992	41	40.23	
5	1.4	1.4	2.8	0.794	35	34.35	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

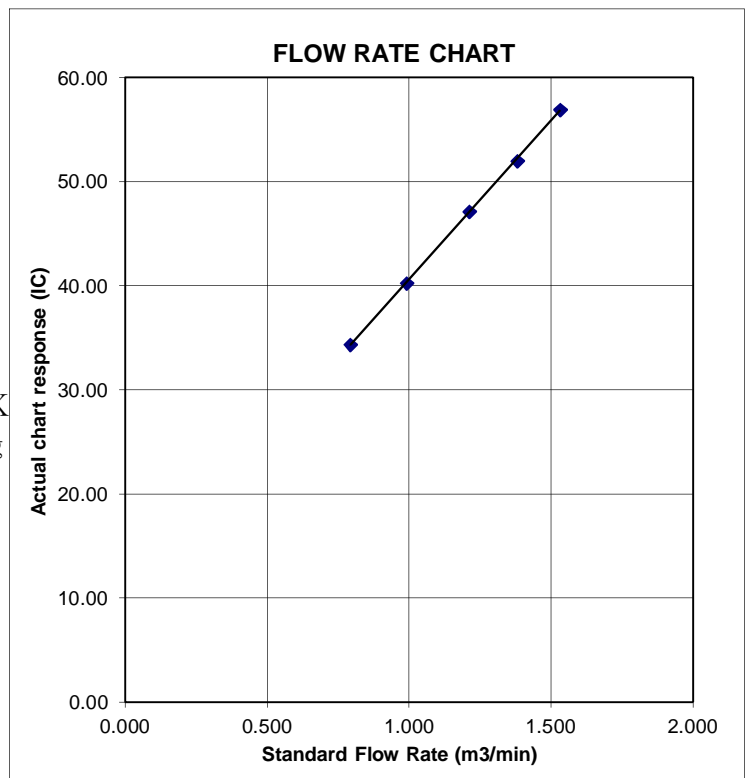

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : YSW Playground
 Location ID : AC04c

Date of Calibration: 1-Aug-11
 Next Calibration Date: 1-Oct-11
 Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa)	1005.5	Corrected Pressure (mm Hg)	754.125
Temperature (°C)	29.5	Temperature (K)	303

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11693
Model->	5025A	Qstd Intercept ->	-0.02568
Serial # ->	1941		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.1	5.1	10.2	1.504	59	57.90	Slope = 32.9377 Intercept = 8.1074 Corr. coeff. = 0.9997
13	4.2	4.2	8.4	1.366	54	52.99	
10	3.2	3.2	6.4	1.194	48	47.10	
7	2.4	2.4	4.8	1.035	43	42.20	
5	1.5	1.5	3	0.821	36	35.33	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

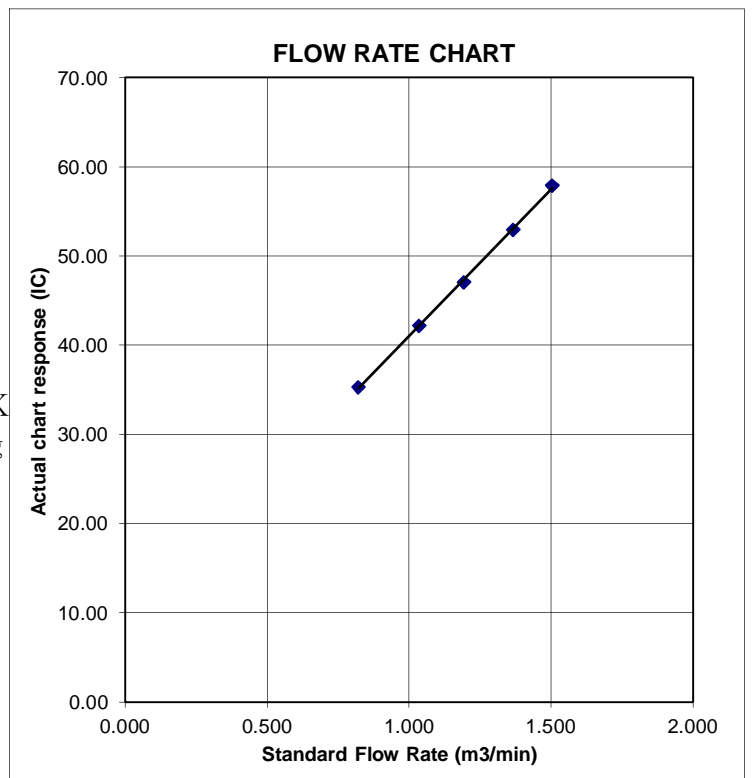




CERTIFICATE OF CALIBRATION AND TESTING

TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA
 Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

Environment Condition			Model	8520
Temperature	73.6 (23.1)	°F (°C)		
Relative Humidity	16	%RH	Serial Number	21060
Barometric Pressure	28.76 (973.9)	inHg (hPa)		

<input checked="" type="checkbox"/> As Left	<input checked="" type="checkbox"/> In Tolerance
<input type="checkbox"/> As Found	<input type="checkbox"/> Out of Tolerance

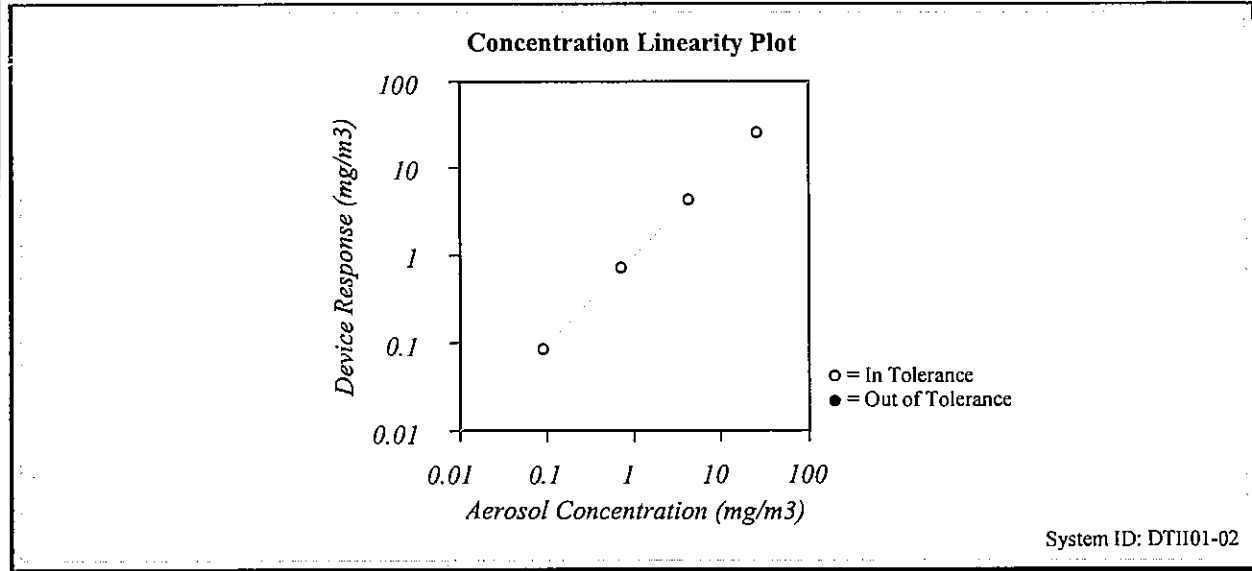

Zero Stability Results			
Average:	Minimum:	Maximum:	Time:
0.000 :mg/m ³	0.000 :mg/m ³	0.001 :mg/m ³	4:00 :hrs.

TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 1.2:1

Measurement Variable	System ID	Last Cal.	Cal. Due	Measurement Variable	System ID	Last Cal.	Cal. Due
Barometric Pressure	E003733	01-15-11	02-15-12	Temperature	E002873	11-24-10	11-24-11
Humidity	E002873	11-24-10	11-24-11	DC Voltage	E003314	01-05-11	01-05-12
DC Voltage	E003315	01-05-11	01-05-12	Photometer	E003319	07-30-10	01-30-11
Microbalance	E001324	01-04-11	01-04-12	Flow and Temperature	E003769	06-15-10	06-15-11
Pressure	E003511	11-12-10	11-12-11				

Final Function Check
 January 27, 2011

Calibrated
Date




CERTIFICATE OF CALIBRATION AND TESTING

TSI Incorporated, 500 Cardigan Road, Shoreview, MN 55126 USA
 Tel: 1-800-874-2811 1-651-490-2811 Fax: 1-651-490-3824 http://www.tsi.com

Environment Condition			Model	8520
Temperature	73.8 (23.2)	°F (°C)		
Relative Humidity	14	%RH	Serial Number	23080
Barometric Pressure	29.41 (995.9)	inHg (hPa)		

<input checked="" type="checkbox"/> As Left	<input checked="" type="checkbox"/> In Tolerance
<input type="checkbox"/> As Found	<input type="checkbox"/> Out of Tolerance

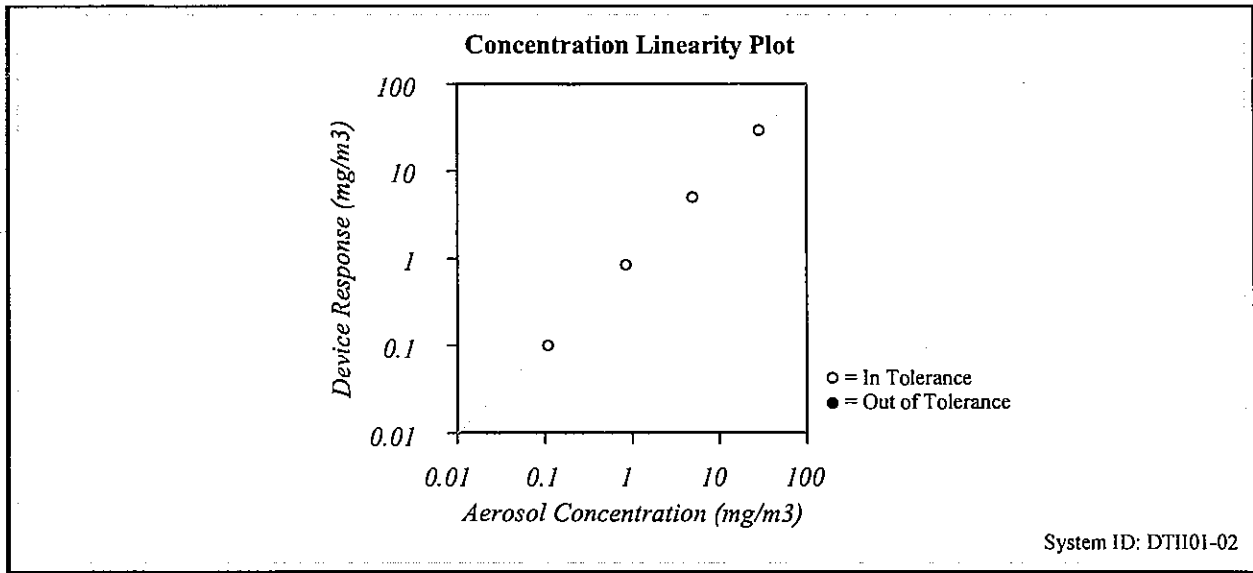

Zero Stability Results			
Average:	Minimum:	Maximum:	Time:
0.000 :mg/m ³	0.000 :mg/m ³	0.001 :mg/m ³	4:00 :hrs.

TSI Incorporated does hereby certify that all materials, components, and workmanship used in the manufacture of this equipment are in strict accordance with the applicable specifications agreed upon by TSI and the customer and with all published specifications. All performance and acceptance tests required under this contract were successfully conducted according to required specifications. There is no NIST standard for optical mass measurements. Calibration of this instrument performed by TSI has been done using emery oil and has been nominally adjusted to respirable mass of standard ISO 12103-1, A1 test dust (Arizona dust). Our calibration ratio is greater than 1.2:1

Measurement Variable	System ID	Last Cal.	Cal. Due	Measurement Variable	System ID	Last Cal.	Cal. Due
Barometric Pressure	E003733	01-15-11	02-15-12	Temperature	E002873	11-24-10	11-24-11
Humidity	E002873	11-24-10	11-24-11	DC Voltage	E003314	01-05-11	01-05-12
DC Voltage	E003315	01-05-11	01-05-12	Photometer	E003319	01-27-11	07-27-11
Microbalance	E001324	01-04-11	01-04-12	Flow and Temperature	E003769	06-15-10	06-15-11
Pressure	E003511	11-12-10	11-12-11				


[Signature]

 Calibrated

Final Function Check

February 1, 2011

 Date



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C112202

Certificate of Calibration

This is to certify that the equipment

Description : Integrating Sound Level Meter (EQ010)

Manufacturer : Bruel & Kjaer

Model No. : 2238

Serial No. : 2285721

*has been calibrated for the specific items and ranges.
The results are shown in the Calibration Report No. C112202.*


The equipment is supplied by

Co. Name : Action-United Environmental Services and Consulting

*Address : Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.*

Date of Issue : 19 April 2011

Certified by :


K C Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited


c/o 4/F, Tsing Shan Wan Exchange Building, I Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C112202

Calibration Report

ITEM TESTED

DESCRIPTION : Integrating Sound Level Meter (EQ010)
MANUFACTURER : Bruel & Kjaer
MODEL NO. : 2238
SERIAL NO. : 2285721

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$ RELATIVE HUMIDITY : $(55 \pm 20)\%$
LINE VOLTAGE : ---

TEST SPECIFICATIONS

Calibration check

DATE OF TEST : 18 April 2011

JOB NO. : IC11-0947

TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested by :


L L Cheung


Date : 19 April 2011

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong
Tel: 2927 2606 Fax: 2744 8986 E-mail: callab@suncreation.com Website: www.suncreation.com

Page 1 of 4



Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration using the B & K Acoustic Calibrator 4231, S/N : 2713428 was performed before the test.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL280	40 MHz Arbitrary Waveform Generator	C110018
CL281	Multifunction Acoustic Calibrator	C1006860

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level


UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L _{AFP}	A	F	94.00	1	94.0	± 0.7

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
50 - 130	L _{AFP}	A	F	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

The test equipment used for calibration are traceable to the National Standards as specified in this report. This report shall not be reproduced except in full and with prior written approval from this laboratory.



Calibration Report

6.2 Time Weighting

6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L _{AFP}	A	F	94.00	1	94.0	Ref.
	L _{ASP}		S			94.0	± 0.1
	L _{AIP}		I			94.1	± 0.1

6.2.2 Tone Burst Signal (2 kHz)


UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
30 - 110	L _{AFP}	A	F	106.0	Continuous	106.0	Ref.
	L _{AFMax}				200 ms	105.0	-1.0 ± 1.0
	L _{ASP}	S	Continuous		106.0	Ref.	
	L _{ASMax}		500 ms		101.9	-4.1 ± 1.0	

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{AFP}	A	F	94.00	31.5 Hz	54.6	-39.4 ± 1.5
					63 Hz	67.7	-26.2 ± 1.5
					125 Hz	77.7	-16.1 ± 1.0
					250 Hz	85.2	-8.6 ± 1.0
					500 Hz	90.7	-3.2 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	95.2	+1.2 ± 1.0
					4 kHz	95.0	+1.0 ± 1.0
					8 kHz	92.8	-1.1 (+1.5 ; -3.0)
					12.5 kHz	89.7	-4.3 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the National Standards as specified in this report. This report shall not be reproduced except in full and with prior written approval from this laboratory.



Calibration Report

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{CFP}	C	F	94.00	31.5 Hz	91.1	-3.0 ± 1.5
					63 Hz	93.2	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.0
					250 Hz	94.0	0.0 ± 1.0
					500 Hz	94.0	0.0 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	93.8	-0.2 ± 1.0
					4 kHz	93.2	-0.8 ± 1.0
					8 kHz	90.9	-3.0 (+1.5 ; -3.0)
					12.5 kHz	87.8	-6.2 (+3.0 ; -6.0)

6.4 Time Averaging

UUT Setting				Applied Value					UUT Reading (dB)	IEC 60804 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)		
30 - 110	L _{Aeq}	A	10 sec.	4	1	1/10	110.0	100	99.9	± 0.5
			60 sec.					90	89.6	± 0.5
			5 min.					80	79.3	± 1.0
								70	69.9	± 1.0

Remarks : - Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1


- Uncertainties of Applied Value :
 - 94 dB : 31.5 Hz - 125 Hz : ± 0.40 dB
 - 250 Hz - 500 Hz : ± 0.30 dB
 - 1 kHz : ± 0.20 dB
 - 2 kHz : ± 0.40 dB
 - 4 kHz : ± 0.50 dB
 - 8 kHz : ± 0.70 dB
 - 12.5 kHz : ± 1.20 dB
 - 104 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
 - 114 dB : 1 kHz : ± 0.10 dB (Ref. 94 dB)
 - Burst equivalent level : ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the National Standards as specified in this report. This report shall not be reproduced except in full and with prior written approval from this laboratory.



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Certificate No. : C112201

Certificate of Calibration

This is to certify that the equipment

Description : Acoustical Calibrator (EQ082)

Manufacturer : Bruel & Kjaer

Model No. : 4231

Serial No. : 2713428

*has been calibrated for the specific items and ranges.
The results are shown in the Calibration Report No. C112201.*

The equipment is supplied by

Co. Name : Action-United Environmental Services and Consulting

*Address : Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.*

Date of Issue : 19 April 2011

Certified by :

K C Lee

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited


c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com



輝創工程有限公司

Sun Creation Engineering Limited Calibration and Testing Laboratory

Report No. : C112201

Calibration Report

ITEM TESTED

DESCRIPTION : Acoustical Calibrator (EQ082)
MANUFACTURER : Bruel & Kjaer
MODEL NO. : 4231
SERIAL NO. : 2713428

TEST CONDITIONS

AMBIENT TEMPERATURE : $(23 \pm 2)^{\circ}\text{C}$ RELATIVE HUMIDITY : $(55 \pm 20)\%$
LINE VOLTAGE : ---

TEST SPECIFICATIONS

Calibration check

DATE OF TEST : 18 April 2011

JOB NO. : IC11-0947


TEST RESULTS

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- The Bruel & Kjaer Calibration Laboratory, Denmark
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested by :


L L Cheung

Date : 19 April 2011

The test equipment used for calibration are traceable to the National Standards as specified in this report.
This report shall not be reproduced except in full and with prior written approval from this laboratory.

Calibration and Testing Laboratory of Sun Creation Engineering Limited

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong


Tel: 2927 2606

Fax: 2744 8986

E-mail: callab@suncreation.com

Website: www.suncreation.com

Page 1 of 2



Calibration Report

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 24 hours before the commencement of the test.
2. The results presented are the mean of 3 measurements at each calibration point.
3. Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C103289
CL281	Multifunction Acoustic Calibrator	C1006860
TST150A	Measuring Amplifier	C101008

4. Test procedure : MA100N.

5. Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.0		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : - The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Calibration Report only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.



ALS Technichem (HK) Pty Ltd

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR BEN TAM
CLIENT: ACTION UNITED ENVIRO SERVICES
ADDRESS: RM A 20/F., GOLDEN KING IND BLDG,
NO. 35-41 TAI LIN PAI ROAD,
KWAI CHUNG,
N.T., HONG KONG.

WORK ORDER: HK1119232
LABORATORY: HONG KONG
DATE RECEIVED: 16/08/2011
DATE OF ISSUE: 17/08/2011

PROJECT: --

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory.
Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of ALS will be followed.

Scope of Test: Dissolved Oxygen, pH, Salinity and Temperature
Description: YSI Professional Plus
Brand Name: YSI
Model No.: YSI Professional Plus
Serial No.: 10G101946
Equipment No.: --
Date of Calibration: 16 August, 2011

NOTES


This is the Final Report and supersedes any preliminary report with this batch number.
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ISSUING LABORATORY: HONG KONG

Address

ALS Technichem (HK) Pty Ltd
11/F Chung Shun Knitting Centre
1-3 Wing Yip Street
Kwai Chung
HONG KONG

Phone: 852-2610 1044
Fax: 852-2610 2021
Email: hongkong@alsglobal.com


Mr Chan Kwok-Fai, Godfrey
Laboratory Manager - Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

Page 1 of 2

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK1119232
Date of Issue: 17/08/2011
Client: ACTION UNITED ENVIRO SERVICES



Description: YSI Professional Plus
Brand Name: YSI
Model No.: YSI Professional Plus
Serial No.: 10G101946
Equipment No.: --
Date of Calibration: 16 August, 2011

Date of next Calibration: 16 November, 2011

Parameters:

Dissolved Oxygen **Method Ref: APHA (21st edition), 4500O: G**

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
4.61	4.76	0.15
6.82	7.00	0.18
8.12	8.31	0.19
Tolerance Limit (\pm mg/L)		0.20

pH Value

Method Ref: APHA (21st edition), 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.00	4.10	0.10
7.00	7.06	0.06
10.00	9.92	-0.08
Tolerance Limit (\pm unit)		0.20

Salinity

Method Ref: APHA (21st edition), 2520B


Expected Reading (g/L)	Displayed Reading (g/L)	Tolerance (%)
0.00	0.00	--
10.00	10.22	2.2
20.00	20.28	1.4
30.00	30.57	1.9
Tolerance Limit (\pm %)		10.0

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical

Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Reading of Ref. thermometer ($^{\circ}$ C)	Displayed Reading ($^{\circ}$ C)	Tolerance ($^{\circ}$ C)
9.5	9.1	-0.4
22.0	21.6	-0.4
35.5	35.1	-0.4
Tolerance Limit ($^{\circ}$ C)		2.0


 Mr Chan Kwok Fai, Godfrey
 Laboratory Manager - Hong Kong



ALS Technichem (HK) Pty Ltd

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR BEN TAM
CLIENT: ACTION UNITED ENVIRO SERVICES
ADDRESS: RM A 20/F., GOLDEN KING IND BLDG,
NO. 35-41 TAI LIN PAI ROAD,
KWAI CHUNG,
N.T., HONG KONG.

WORK ORDER: HK1120797
LABORATORY: HONG KONG
DATE RECEIVED: 06/09/2011
DATE OF ISSUE: 08/09/2011

PROJECT: --

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory.
Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of ALS will be followed.

Scope of Test: Turbidity
Description: Turbidimeter
Brand Name: HACH
Model No.: 2100P
Serial No.: 950900008735
Equipment No.: --
Date of Calibration: 06 September, 2011

NOTES


This is the Final Report and supersedes any preliminary report with this batch number.
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ISSUING LABORATORY: HONG KONG

Address

ALS Technichem (HK) Pty Ltd
11/F Chung Shun Knitting Centre
1-3 Wing Yip Street
Kwai Chung
HONG KONG

Phone: 852-2610 1044
Fax: 852-2610 2021
Email: hongkong@alsglobal.com


Mr Chan Kwok Fai, Godfrey
Laboratory Manager - Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

Page 1 of 2

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

Work Order: HK1120797
Date of Issue: 08/09/2011
Client: ACTION UNITED ENVIRO SERVICES




Description: Turbidimeter
Brand Name: HACH
Model No.: 2100P
Serial No.: 950900008735
Equipment No.: --
Date of Calibration: 06 September, 2011 Date of next Calibration: 06 December, 2011

Parameters:

Turbidity

Method Ref: ALPHA 21st Ed. 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0.00	0.23	--
4.00	3.83	-4.3
40.0	38.4	-4.0
80.0	82.1	2.6
400	408	2.0
800	802	0.3
	Tolerance Limit ($\pm\%$)	10.0


Mr. Chan Kwok Fai, Godfrey
Laboratory Manager - Hong Kong



Hong Kong Accreditation Service
香港認可處

Certificate of Accreditation
認可證書

This is to certify that
特此證明

ALS TECHNICHEM (HK) PTY LIMITED

11/F., Chung Shun Knitting Centre, 1-3 Wing Yip Street, Kwai Chung, New Territories, Hong Kong
香港新界葵涌永業街1-3號忠信針織中心11樓

has been accepted by the HKAS Executive, on the recommendation of the Accreditation Advisory Board, as a
為香港認可處執行機關根據認可諮詢委員會建議而接受的

HOKLAS Accredited Laboratory
「香港實驗所認可計劃」認可實驗所

This laboratory meets the requirements of ISO / IEC 17025 : 2005 – General requirements for the competence of testing and calibration laboratories and it has been accredited for performing specific tests or calibrations as listed in the HOKLAS Directory of Accredited Laboratories within the test category of
此實驗所符合ISO / IEC 17025 : 2005 –《測試及校正實驗所能力的通用規定》所訂的要求，獲認可進行載於香港實驗所認可計劃《認可實驗所名冊》內下述測試類別中的指定
測試或校正工作

Environmental Testing
環境測試

This laboratory is accredited in accordance with the recognised International Standard ISO / IEC 17025 : 2005.
本實驗所乃根據公認的國際標準 ISO / IEC 17025 : 2005 獲得認可。

This accreditation demonstrates technical competence for a defined scope and the operation of a laboratory quality management system (see joint IAF-ILAC-ISO Communiqué).
這項認可資格演示在指定範疇所需的技術能力及實驗所質量管理體系的運作
(見國際認可論壇、國際實驗所認可合作組織及國際標準化組織的聯合公報)。

The common seal of the Hong Kong Accreditation Service is affixed hereto by the authority of the HKAS Executive
香港認可處根據認可處執行機關的權限在此蓋上通用印章

CHAN Sing Sing, Terence, Executive Administrator
執行幹事 陳成城
Issue Date : 5 May 2009
簽發日期：二零零九年五月五日

Registration Number : **HOKLAS 066**
註冊號碼：

Date of First Registration : 15 September 1995
首次註冊日期：一九九五年九月十五日



Appendix F

Event and Action Plan

Air Quality

EVENT	ACTION	IC(E)	ER	CONTRACTOR
	ET			
ACTION LEVEL				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IC(E) and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IC(E) and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IC(E) and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IC(E) and ER; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
LIMIT LEVEL				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IC(E), ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IC(E) and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IC(E), agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Construction Noise

EVENT	ACTION			
	ET	IC(E)	ER	CONTRACTOR
Action Level	<ol style="list-style-type: none"> 1. Notify IC(E) and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IC(E), ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IC(E); 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IC(E), ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IC(E), ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Water Quality

EVENT	ACTION			
	ET	IC(E)	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sampling day	<ol style="list-style-type: none"> Repeat in-situ measurement on the next day of exceedance to confirm findings; Identify source(s) of impact; Inform ICE, Contractor, ER, EPD and AFCD; and Check monitoring data, all plant, equipment and Contractor's working methods. 	<ol style="list-style-type: none"> Check monitoring data submitted by ET and Contractor's working methods 	<ol style="list-style-type: none"> Confirm receipt of notification of non-compliance in writing; and Notify Contractor 	<ol style="list-style-type: none"> Information the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; and Amend working methods if appropriate
2. Exceedance for two or more consecutive sampling days	<ol style="list-style-type: none"> Same as the above; Inform ICE, Contractor, ER, EPD and AFCD; Discuss mitigation measures with IC(E), RE and Contractor; Ensure well implementation of mitigation measures; and Increase the monitoring frequency to daily until no exceedance of Action Level 	<ol style="list-style-type: none"> Same as the above; Discuss with ET and Contractor on possible remedial actions; Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; and Supervise the implementation of mitigation measures. 	<ol style="list-style-type: none"> Discuss with IC(E) on the proposed mitigation measures; Ensure well implementation of mitigation measures; and Assess the effectiveness of the implemented mitigation measures 	<ol style="list-style-type: none"> Same as the above; Check all plant and equipment and consider changes of working methods; Submit proposal of additional mitigation measures to ER within 3 working days of notification and discuss with ET, IC(E), and ER; and Implement the agreed mitigation measures
LIMIT LEVEL				
1. Exceedance for one sampling day	<ol style="list-style-type: none"> Repeat in-situ measurement on the next day of exceedance to confirm findings; Identify source(s) of impact; Inform ICE, Contractor, ER, EPD and AFCD; Check monitoring data, all plant, equipment and Contractor's working methods; and Discuss mitigation measures with IC(E), RE and Contractor 	<ol style="list-style-type: none"> Check monitoring data submitted by ET and Contractor's working method Discuss with ER and Contractor on possible remedial actions; and Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly 	<ol style="list-style-type: none"> Confirm receipt of notification failure in writing; and Discuss with IC(E), ET and Contractor on the proposed mitigation measures; and Request Contractor to review the working methods 	<ol style="list-style-type: none"> Inform the ER and confirm notification of the failure in writing; Rectify unacceptable practice; Check all plant and equipment and consider changes of working methods; and Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET and ER
2. Exceedance for two or more consecutive sampling days	<ol style="list-style-type: none"> Same as the above; Ensure mitigation measures are implemented; and Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days 	<ol style="list-style-type: none"> Same as the above; and Supervise the Implementation of mitigation measures 	<ol style="list-style-type: none"> Same as the above; Ensure well implementation of mitigation measures Make agreement on the mitigation measures to be implemented; and Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of limit level 	<ol style="list-style-type: none"> Same as the above; Take immediate action to avoid further exceedance; Implement the agreed mitigation measures; Resubmit proposals of mitigation measures if problem still not under control; and As directed by the Engineer, to slow down or to stop all or part of the construction activities until to no exceedance of Limit Level.

Coral Monitoring

EVENT	ACTION		
	ET	CONTRACTOR	ER/ IC(E)
Action Level being exceeded	<p>Inform contractor, AFCD and EPD immediately;</p> <p>Discuss mitigation measure with ER/IC(E) and Contractor;</p> <p>Ensure mitigation measures are implemented.</p>	<p>Inform the Engineer and confirm notification of the non-compliance in writing;</p> <p>Propose mitigation measure to ER/IC(E) within 1 working day and discuss with Et and ER/IC(E);</p> <p>Ensure mitigation measures are implemented.</p>	<p>Inform contractor, Review water quality monitoring data;</p> <p>Determine whether water quality monitoring data shows effects attributable to the backfilling works;</p> <p>If water quality monitoring data indicates effects attributable to backfilling works, then make agreement on mitigation measures to be implemented;</p> <p>If water quality monitoring data indicates no effects attributable to backfilling works then Action Level is not triggered;</p> <p>Assess the effectiveness of the implemented mitigation measures.</p>
Limit Level	<p>Inform contractor, AFCD and EPD immediately;</p> <p>Discuss mitigation measure with ER/IC(E) and Contractor;</p> <p>Ensure mitigation measures are implemented.</p>	<p>Inform the Engineer and confirm notification of the non-compliance in writing;</p> <p>Suspend backfilling operations;</p> <p>Propose mitigation measure to ER/IC(E) within 3 working days and discuss with Et and ER/IC(E);</p> <p>Implement the agreed mitigation measures.</p>	<p>Inform contractor to suspend backfilling operations;</p> <p>Make agreement on the mitigation measures to be implemented;</p> <p>Assess the effectiveness of the implemented mitigation measures.</p>

Appendix G

Monitoring Data Sheet

24-hour TSP Monitoring Data Sheet

Air Quality Monitoring - 24-hour TSP monitoring data for Yung Shue Wan

24-hour TSP Monitoring Results - AC02b

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (oC)	STANDARD			INITIAL FILTER WEIGHT (g)	FINAL FILTER WEIGHT (g)	WEIGHT DUST COLLECTED (g)	DUST 24-hour TSP IN AIR (ug/m ³)
		INITIAL	FINAL	ACTUAL (min)	MIN	MAX	AVG		AVG PRESS (hPa)	FLOW RATE (m3/min)	AIR VOLUME (std m3)				
6-Sep-11	24187	4309.48	4332.96	1408.80	29	34	31.5	29.3	1007.4	0.69	975	2.8481	2.8789	0.0308	32
12-Sep-11	24200	4332.96	4356.44	1408.80	30	34	32.0	28.5	1010.6	0.71	1002	2.8106	2.8658	0.0552	55
17-Sep-11	24217	4356.44	4380.27	1429.80	30	34	32.0	29.4	1004.5	0.71	1010	2.7776	2.822	0.0444	44
23-Sep-11	24222	4380.27	4404.21	1436.40	30	33	31.5	25.6	1009.7	0.70	1005	2.7834	2.9376	0.1542	153
29-Sep-11	24253	4404.21	4427.99	1426.80	30	32	31.0	27.2	1002.9	0.68	966	2.7458	2.8057	0.0599	62

24-hour TSP Monitoring Results - AC04c

DATE	SAMPLE NUMBER	ELAPSED TIME			CHART READING			AVG TEMP (oC)	STANDARD			INITIAL FILTER WEIGHT (g)	FINAL FILTER WEIGHT (g)	WEIGHT DUST COLLECTED (g)	DUST 24-hour TSP IN AIR (ug/m ³)
		INITIAL	FINAL	ACTUAL (min)	MIN	MAX	AVG		AVG PRESS (hPa)	FLOW RATE (m3/min)	AIR VOLUME (std m3)				
6-Sep-11	24188	6876.35	6900.32	1438.20	30	33	31.5	29.3	1007.4	0.70	1008	2.8427	2.8971	0.0544	54
12-Sep-11	24197	6900.32	6924.08	1425.60	29	32	30.5	28.5	1010.6	0.67	960	2.8072	2.8505	0.0433	45
17-Sep-11	24070	6924.08	6947.56	1408.80	30	33	31.5	29.4	1004.5	0.70	985	2.8095	2.8343	0.0248	25
23-Sep-11	24223	6947.56	6971.19	1417.80	30	34	32.0	25.6	1009.7	0.72	1025	2.7771	2.8826	0.1055	103
29-Sep-11	24250	6971.19	6994.96	1426.20	29	33	31.0	27.2	1002.9	0.69	979	2.7802	2.8335	0.0533	54

Marine Water Quality Monitoring Data Sheet

Contract No. DC/2009/13

**Construction of Sewage Treatment Works
at Yung Shue Wan and Sok Kwu Wan**



Marine Water Quality Monitoring Result at Yung Shue Wan

Date 1-Sep-11

Date / Time	Location	Tide	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2011/9/1 13:42	WY1	ME	829165	809558	4.4	1.034	29.30	6.76	94.9	3.0	29.62	8.05	4.7
						1.021	29.20	6.51	93.2	3.4	29.42	8.12	
						3.417	28.30	6.29	89.9	2.7	32.36	7.98	
						3.382	28.30	6.01	88.1	2.8	32.59	8.08	
2011/9/1 14:14	WY2	ME	829000	810424	7.4	1.085	29.30	6.84	95.2	3.4	28.72	8.11	4.2
						1.044	29.20	6.62	94.1	3.6	28.88	8.04	
						3.775	28.60	6.32	91.7	3.7	29.22	8.09	3.8
						3.686	28.60	6.24	93.6	3.1	29.46	8.15	
						6.402	28.40	6.02	93.9	3.2	32.54	8.02	4.4
						6.295	28.20	6.06	90.8	3.3	32.42	8.06	
2011/9/1 13:59	WY3	ME	829222	809880	4.2	1.016	29.40	5.91	87.9	2.6	30.51	8.05	3.3
						0.973	29.40	5.94	87.2	2.9	30.55	7.98	
						3.294	28.50	5.76	85.5	2.8	33.56	8.13	2.7
						3.157	28.50	5.62	84.8	3.2	33.36	8.04	
2011/9/1 14:36	CY1	ME	828419	81814	12.4	0.957	28.60	7.14	98.9	2.9	28.74	7.89	5
						1.006	28.60	7.04	96.4	2.7	28.94	7.96	
						6.196	28.40	5.99	86.2	2.6	30.25	7.97	2.6
						6.261	28.40	5.84	88.1	2.8	30.32	8.04	
						11.383	28.10	5.61	86.5	3.0	32.66	7.94	2.8
						11.405	28.10	5.72	83.4	3.3	32.61	8.01	
2011/9/1 14:58	CY2	ME	828024	808815	17.6	1.043	29.40	6.49	91.4	3.1	28.21	8.03	4.4
						0.951	29.40	6.34	92.8	3.4	28.31	8.12	
						8.842	28.70	6.21	90.0	3.2	30.84	8.17	5.3
						8.795	28.80	6.19	89.7	3.3	30.97	8.09	
						16.594	28.40	5.82	83.2	3.5	33.47	8.13	4.3
						16.553	28.50	5.62	81.8	3.6	33.61	8.06	
2011/9/1 7:36	WY1	MF	829175	809555	4.6	1.026	28.90	6.84	94.6	3.2	29.02	7.92	4.3
						0.992	28.90	6.77	95.8	3.3	28.86	7.97	
						3.638	28.60	6.16	91.3	3.0	30.94	7.99	5.1
						3.620	28.60	6.43	93.2	3.2	31.16	8.05	
2011/9/1 8:06	WY2	MF	829000	810425	7.2	0.996	29.20	7.13	98.3	2.5	28.57	8.11	5.4
						0.999	29.20	7.06	97.1	2.7	28.82	8.03	
						3.668	29.00	6.83	94.8	2.9	29.28	8.06	2.8
						3.596	29.00	6.76	95.6	2.6	29.31	7.97	
						6.196	28.90	6.77	93.3	3.0	33.36	7.94	3
						6.217	28.80	6.62	93.2	2.8	33.16	7.97	
2011/9/1 7:51	WY3	MF	829224	809872	4.8	0.987	28.90	6.23	92.6	2.8	28.32	8.02	3.3
						1.005	28.90	6.36	92.9	2.9	28.42	7.96	
						3.772	28.40	5.56	86.4	3.0	32.64	7.89	3.8
						3.811	28.30	5.72	86.8	2.7	32.55	7.96	
2011/9/1 8:24	CY1	MF	828432	810821	12.2	1.082	29.50	7.23	96.9	3.6	29.92	7.99	4.8
						1.022	29.50	7.02	95.3	3.1	29.58	8.05	
						6.190	29.10	6.83	94.4	3.3	31.62	8.13	12
						6.236	29.10	6.93	93.6	3.5	31.36	8.07	
						11.239	28.50	6.72	92.8	3.7	33.49	8.09	5.4
						11.184	28.50	6.62	91.1	3.3	33.62	8.11	
2011/9/1 8:52	CY2	MF	828025	808822	17.3	1.067	30.10	7.34	92.1	3.8	29.74	7.93	5.5
						1.019	30.60	7.16	90.8	3.9	29.56	7.86	
						8.661	29.40	6.17	89.4	3.3	30.36	7.96	3.5
						8.469	28.90	5.96	88.1	3.5	30.74	7.99	
						16.834	28.30	5.83	84.3	3.6	33.62	8.01	4.3
						16.415	28.10	5.62	82.6	3.7	33.52	7.95	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 3-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2011/9/3 15:36	WY1	ME	829160	809572	4.7	1.113	29.80	6.74	92.1	2.9	30.06	8.00	4.6
						1.041	29.80	6.62	91.6	3.0	30.32	7.90	
						3.652	29.20	6.32	90.3	3.1	31.42	7.80	
						3.718	29.10	6.16	90.9	3.3	31.96	7.90	
2011/9/3 16:07	WY2	ME	829028	810427	7.7	1.088	29.20	7.01	89.4	2.9	29.87	7.80	6.4
						1.004	29.10	6.83	89.9	2.8	29.75	7.90	
						3.895	28.50	6.81	88.9	3.0	31.65	7.90	6.9
						3.806	28.50	6.62	84.2	3.3	31.55	7.80	
						6.827	28.10	6.61	93.8	3.1	31.55	8.00	
						6.743	28.10	6.46	91.4	3.3	31.58	8.00	
2011/9/3 15:49	WY3	ME	829220	809865	4.9	1.055	28.60	6.82	92.8	2.9	29.55	7.90	3.8
						0.989	28.70	6.62	92.6	3.1	29.62	8.00	
						3.841	28.10	6.76	90.6	3.1	31.22	7.80	4.3
						3.886	28.10	6.43	90.2	3.0	31.62	7.90	
2011/9/3 16:24	CY1	ME	828385	810781	12	1.037	28.60	6.83	92.1	2.8	29.52	8.10	2.3
						0.994	28.60	6.69	90.9	2.9	29.59	8.00	
						5.896	28.30	6.16	94.4	3.0	30.86	8.00	4.2
						6.016	28.30	5.91	92.1	3.1	30.88	8.00	
						11.046	28.20	6.34	92.9	3.2	32.22	7.90	
						10.983	28.20	6.28	90.0	3.4	32.15	8.00	
2011/9/3 16:58	CY2	ME	828015	808780	17.4	1.154	29.80	6.46	89.3	2.5	30.32	7.90	6.3
						1.026	29.70	6.32	87.2	2.7	30.32	7.90	
						8.649	29.50	6.39	93.3	2.6	30.99	8.00	4.2
						8.688	29.60	6.28	94.2	2.7	31.22	7.90	
						16.322	28.30	6.16	91.6	2.7	31.89	7.80	
						16.381	28.40	6.03	91.3	2.9	31.99	7.90	
2011/9/3 9:36	WY1	MF	829161	809530	4.9	1.109	29.10	6.81	92.4	3.3	30.30	8.20	7.8
						1.042	28.40	6.79	91.8	3.1	30.60	8.20	
						3.854	28.30	6.32	93.6	3.4	31.20	8.10	6.6
						3.901	27.90	6.21	93.2	3.0	31.25	8.20	
2011/9/3 9:58	WY2	MF	829012	810394	7.6	1.016	30.10	7.06	99.8	3.1	29.40	8.20	6.9
						0.985	30.20	7.03	98.1	2.7	29.20	8.10	
						3.759	29.80	6.79	95.4	2.5	30.40	8.10	6.3
						3.741	29.60	6.72	93.8	3.1	30.45	8.10	
						6.624	28.60	6.62	94.2	2.6	32.20	8.20	
						6.608	28.10	6.32	92.4	3.2	32.40	8.10	
2011/9/3 9:48	WY3	MF	829195	809845	4.2	1.038	30.20	6.32	94.2	3.5	29.80	7.90	9.2
						0.994	30.40	6.16	93.6	3.1	29.80	7.80	
						3.216	29.80	6.82	96.2	3.3	30.60	7.80	17
						3.175	29.40	6.61	94.8	2.9	30.40	7.80	
2011/9/3 10:21	CY1	MF	828397	810789	12.8	1.082	28.60	6.28	93.8	2.7	29.30	8.00	7.5
						1.019	28.60	6.21	92.6	3.0	29.55	7.90	
						6.388	28.40	6.16	92.4	2.9	30.56	7.90	4.9
						6.405	28.40	6.10	90.1	2.8	30.49	7.90	
						11.778	28.20	6.21	90.9	3.0	31.88	7.90	
2011/9/3 10:56	CY2	MF	828005	808794	17.1	11.912	28.20	6.14	89.6	2.9	31.94	8.00	8.2
						1.162	29.90	7.04	99.1	3.1	28.30	8.10	
						1.057	30.10	7.01	97.6	3.0	28.90	8.10	6.5
						8.374	29.20	6.86	96.2	2.8	30.30	8.20	
						8.512	29.30	6.62	95.4	3.1	30.90	8.10	
						16.057	28.00	6.56	95.8	2.7	31.60	8.10	
16.084	27.90	6.42	94.2	3.0	31.30	8.00	4.6						

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 5-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2011/9/5 17:19	WY1	ME	829158	809570	4.8	1.105	29.40	6.56	93.0	3.8	29.36	7.80	9.7
						1.043	29.30	6.32	93.2	3.8	28.67	7.90	
						3.782	28.80	6.36	92.8	3.4	30.41	7.60	
						3.817	28.90	6.16	91.9	3.1	30.52	7.70	
2011/9/5 17:42	WY2	ME	829021	810419	7.3	1.082	29.60	6.49	89.1	3.2	29.43	8.00	3.2
						1.011	29.80	6.39	92.1	3.1	29.74	8.00	
						3.669	29.40	6.28	92.9	3.4	30.36	8.10	3
						3.607	29.10	6.26	91.9	3.3	30.81	8.00	
						6.287	28.80	6.17	89.1	3.1	31.62	8.10	
						6.325	28.70	6.11	96.2	3.3	31.77	8.10	
2011/9/5 17:28	WY3	ME	829415	810811	4.4	1.074	29.10	6.52	94.3	3.0	28.31	7.80	3.1
						0.996	29.10	6.36	93.8	2.9	29.42	7.90	
						3.419	28.40	6.24	90.8	3.0	30.31	7.80	3.8
						3.385	28.50	6.21	90.1	3.3	30.49	7.80	
2011/9/5 17:56	CY1	ME	828419	810822	12.4	1.041	29.30	6.07	93.3	3.2	29.42	7.90	2.6
						0.983	29.40	6.01	91.9	3.1	29.91	7.80	
						6.254	28.90	5.96	89.8	3.4	30.61	7.90	3
						6.191	28.90	5.83	94.8	3.3	30.16	8.00	
						11.386	28.20	5.72	96.3	3.3	32.34	8.00	
11.412	28.20	5.61	94.4	3.2	32.28	8.00							
2011/9/5 17:02	CY2	ME	828015	808798	17.4	1.112	30.30	6.82	92.6	2.8	29.94	8.00	2.5
						1.035	30.10	6.64	93.1	2.9	28.83	7.90	
						8.696	28.80	6.24	95.2	3.0	30.32	7.90	3.8
						8.715	28.80	6.16	93.2	3.3	31.43	7.90	
						16.427	28.10	6.07	91.6	2.8	31.42	7.90	
						16.409	28.80	6.02	92.8	2.4	31.36	8.00	
2011/9/5 12:58	WY1	MF	829160	809572	4.5	1.021	29.30	6.24	94.8	2.8	29.30	8.00	6.5
						0.989	29.40	6.32	92.3	2.7	29.60	8.00	
						3.516	27.90	6.16	92.6	3.0	30.30	8.10	3.3
						3.489	27.90	6.02	90.8	2.9	30.20	8.00	
2011/9/5 13:17	WY2	MF	828981	810398	7.8	1.064	29.30	6.88	91.9	2.8	29.40	8.00	6.8
						1.002	29.20	6.81	90.9	2.8	29.30	7.90	
						3.952	28.90	6.82	95.7	2.8	30.80	7.70	4.7
						3.917	28.80	6.61	94.3	3.0	30.30	7.80	
						6.822	28.20	6.49	93.8	2.6	31.40	8.10	6.3
						6.798	28.20	6.56	93.6	2.6	31.60	8.00	
2011/9/5 12:58	WY3	MF	829182	809877	4.7	1.055	28.70	6.42	92.8	3.1	29.30	7.80	2
						1.016	28.70	6.37	96.3	3.0	29.80	7.90	
						3.694	28.10	6.02	94.1	3.2	30.60	7.90	4.7
						3.711	28.20	6.16	91.6	3.1	30.30	7.80	
2011/9/5 13:36	CY1	MF	828395	810791	12.8	1.033	29.60	6.73	91.2	2.8	28.30	8.10	1.7
						0.996	29.50	6.53	93.2	2.7	29.20	8.10	
						6.418	28.50	6.16	91.6	3.1	30.60	8.00	4.8
						6.386	28.50	6.04	99.2	3.0	30.10	8.10	
						11.754	28.10	5.83	90.3	3.2	31.40	8.00	4.1
						11.793	28.10	6.01	92.8	3.1	31.80	8.10	
2011/9/5 13:58	CY2	MF	828017	808800	17.3	1.009	28.90	6.66	92.8	3.2	29.40	7.80	9.5
						0.941	28.90	6.55	91.3	3.3	29.30	7.90	
						8.751	28.10	6.43	90.6	3.3	30.80	8.10	9.6
						8.669	28.10	6.28	90.8	3.4	30.80	8.00	
						16.284	27.50	6.33	94.9	3.3	31.30	8.20	6.9
						16.311	27.50	6.16	93.2	3.0	31.20	8.10	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 7-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2011/9/7 8:42	WY1	ME	829155	809572	4.3	1.060	28.80	6.72	93.6	3.2	29.46	8.10	8.4
						1.003	28.80	6.32	92.3	3.2	29.55	8.00	
						3.295	28.40	6.16	94.2	3.8	30.23	8.10	
						3.317	28.40	5.99	93.8	3.7	30.22	8.00	
2011/9/7 9:16	WY2	ME	829020	810397	7.3	1.154	29.10	6.49	95.2	3.2	28.22	8.00	8.8
						1.042	29.10	6.36	95.1	3.3	28.10	7.90	
						3.682	28.70	6.16	97.6	3.4	29.13	7.90	4.4
						3.647	28.70	6.09	96.8	3.6	29.22	8.00	
						6.318	28.40	6.04	94.2	3.4	30.65	7.80	
						6.290	28.40	6.02	94.1	3.2	30.64	7.90	
2011/9/7 8:58	WY3	ME	829215	809876	4.6	1.106	28.90	6.31	92.6	4.0	27.98	8.20	4.1
						1.031	28.90	6.28	90.9	4.4	27.88	8.10	
						3.585	28.50	6.16	91.3	4.3	31.22	8.00	8.4
						3.609	28.50	6.14	90.2	4.6	31.20	8.00	
2011/9/7 9:32	CY1	ME	828384	810826	12.1	1.042	28.70	6.34	93.1	3.1	28.20	7.90	2.4
						0.996	28.70	6.32	93.8	3.2	28.13	7.90	
						6.074	28.50	6.31	93.3	3.7	30.00	8.00	3
						6.005	28.50	6.28	92.8	3.9	30.21	7.90	
						11.065	28.10	6.03	92.8	4.5	31.26	8.20	
						11.041	28.10	6.01	91.1	4.0	31.55	8.10	
2011/9/7 8:21	CY2	ME	828020	808800	17.2	1.053	29.10	6.82	93.8	4.1	28.10	8.00	5.2
						1.011	29.10	6.86	95.2	4.3	28.22	7.90	
						8.624	28.70	6.72	90.2	3.8	29.64	8.00	4.6
						8.591	28.70	6.51	94.2	3.2	29.46	8.10	
						16.186	28.20	6.32	92.6	2.5	31.55	8.10	
						16.209	28.20	6.36	91.3	2.6	31.80	8.10	
2011/9/7 15:56	WY1	MF	829158	809564	4.3	1.044	29.20	6.12	94.8	3.1	28.55	8.10	9.2
						0.997	29.20	6.24	93.2	3.3	28.68	8.00	
						3.305	28.40	6.01	89.9	3.6	30.22	8.10	12.6
						3.286	28.40	6.00	89.1	3.6	30.16	8.00	
2011/9/7 16:24	WY2	MF	829015	810395	7.7	1.008	29.10	6.86	89.1	3.2	30.50	7.80	4.7
						0.985	29.10	6.86	87.7	3.2	30.56	7.90	
						3.821	28.50	6.86	85.8	3.1	31.20	8.00	3.1
						3.844	28.50	6.72	86.5	3.1	31.22	7.90	
						6.686	28.10	6.43	89.6	3.6	31.89	7.80	
						6.712	28.20	6.16	85.6	3.6	31.99	7.90	
2011/9/7 16:12	WY3	MF	829218	809876	4.1	1.031	28.80	6.36	90.8	3.6	29.50	8.00	7.8
						0.995	28.80	6.62	90.1	2.2	29.23	8.10	
						3.131	28.40	6.16	91.6	3.6	30.22	8.00	9
						3.982	28.40	6.32	91.3	3.6	30.52	7.90	
2011/9/7 16:42	CY1	MF	828391	810818	12.1	1.059	29.10	6.72	92.4	3.2	30.11	7.90	4.1
						1.004	29.00	6.81	95.2	3.2	30.12	8.00	
						6.102	28.40	6.16	92.8	3.6	31.22	8.10	3
						6.072	28.40	6.07	91.9	3.6	31.14	8.00	
						11.123	28.10	5.62	92.9	3.6	32.00	8.10	
						11.089	28.00	5.16	92.9	3.6	32.02	8.00	
2011/9/7 15:42	CY2	MF	827992	808814	17.6	1.077	29.30	6.56	92.4	4.2	29.10	8.00	6.1
						1.015	29.40	6.76	90.3	4.2	29.20	8.10	
						8.776	28.40	6.08	91.6	5.2	30.56	8.00	1.9
						8.802	28.40	6.19	90.1	5.2	30.41	7.90	
						16.569	28.00	5.94	94.3	3.9	31.55	7.90	
						16.594	28.80	5.74	93.7	3.9	31.68	8.00	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 9-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2011/9/9 9:58	WY1	ME	829162	809565	4.3	1.059	29.20	7.01	90.4	4.7	30.23	8.00	7.1
						1.012	29.10	7.02	90.1	4.9	30.60	8.10	
						3.327	28.20	6.62	89.2	4.8	31.30	8.10	11.8
						3.305	28.00	6.42	89.4	4.0	31.20	8.10	
2011/9/9 10:19	WY2	ME	829019	810381	7.7	1.051	28.10	6.74	98.3	4.2	28.80	8.00	7.4
						1.004	28.00	6.82	98.2	4.3	29.20	8.10	
						3.872	27.90	6.67	96.4	4.4	30.20	8.10	10.3
						3.851	27.20	6.58	96.0	4.4	30.10	8.00	
						6.729	26.80	6.54	95.2	4.3	31.22	8.30	8.8
						6.695	26.70	6.32	95.1	4.7	31.20	8.10	
2011/9/9 10:06	WY3	ME	829198	809835	4.2	1.020	29.10	6.76	89.4	3.9	29.60	8.00	12.2
						0.991	29.00	6.56	89.2	4.7	29.80	8.00	
						3.184	27.20	6.92	89.4	4.9	30.10	7.90	9
						3.196	27.10	6.86	89.2	4.8	30.20	8.00	
2011/9/9 10:36	CY1	ME	828395	810826	13.1	1.016	27.90	6.87	94.3	4.3	28.90	8.20	10
						0.983	27.90	6.72	94.2	3.8	28.80	8.10	
						6.547	26.90	6.96	93.8	4.8	30.10	8.20	5.9
						6.495	26.20	6.92	93.2	4.0	30.20	8.30	
						12.098	26.20	6.72	92.6	3.9	30.50	8.10	5.2
						12.073	26.60	6.71	92.3	3.9	30.60	8.10	
2011/9/9 9:42	CY2	ME	828019	808818	17.6	1.035	28.70	6.56	95.4	4.7	30.10	7.90	3.9
						0.999	28.60	6.86	93.2	4.9	30.20	8.00	
						8.787	27.60	6.56	92.8	4.8	30.80	8.00	5.4
						8.809	27.30	5.96	91.6	4.8	30.80	7.90	
						16.615	26.20	7.06	89.2	3.8	32.50	8.10	4.3
						15.963	26.30	7.01	89.2	3.9	32.66	8.00	
2011/9/9 16:43	WY1	MF	829151	809531	4.2	1.031	29.70	6.24	88.2	4.6	30.10	8.00	8.9
						0.994	28.20	6.04	87.8	4.2	30.20	8.10	
						3.201	26.10	6.51	88.6	4.4	33.10	8.10	6.2
						3.174	25.80	6.32	86.2	4.8	33.10	8.20	
2011/9/9 17:16	WY2	MF	828998	810418	7.8	1.049	28.30	6.92	88.6	3.4	29.50	8.00	4.3
						1.002	28.10	6.86	84.2	3.5	29.60	8.00	
						3.825	27.10	6.26	88.2	3.5	30.70	8.10	4.6
						3.879	27.00	6.16	88.4	4.4	30.70	8.10	
						6.755	26.90	5.92	82.6	4.4	31.80	8.00	4.6
						6.930	26.80	5.82	81.8	4.9	31.90	8.10	
2011/9/9 16:59	WY3	MF	829180	809876	4.4	1.112	25.80	6.26	87.8	3.9	30.10	8.20	3.6
						1.027	25.10	6.13	85.2	5.4	30.90	8.10	
						3.419	24.10	6.31	89.2	3.2	32.50	8.10	4.2
						3.386	24.00	6.26	89.4	3.2	32.40	8.10	
2011/9/9 17:28	CY1	MF	828419	810819	13.0	1.066	28.20	6.72	83.1	4.6	29.80	8.40	2.9
						1.013	27.10	6.71	81.7	4.7	29.40	8.30	
						6.548	26.60	6.62	87.4	4.9	30.10	8.30	4.8
						6.515	26.20	6.58	87.2	4.9	30.20	8.20	
						12.054	26.10	6.59	86.2	4.9	31.60	8.30	6.6
						11.869	25.90	6.42	87.8	4.8	31.60	8.20	
2011/9/9 16:32	CY2	MF	828012	808810	17.1	1.032	28.60	6.62	95.9	4.2	29.20	8.00	6.7
						0.997	29.20	6.56	92.6	4.3	29.20	8.10	
						8.584	27.30	6.56	92.8	4.4	30.50	8.10	4.1
						8.601	27.90	6.16	91.3	4.3	30.60	8.00	
						16.082	26.60	6.02	89.2	4.3	31.10	8.30	4.6
						16.119	26.80	5.96	89.4	4.6	31.20	8.20	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 12-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2011/9/12 12:08	WY1	ME	829150	809566	4.2	1.087	29.20	6.03	86.2	5.8	28.00	8.10	8
						1.015	28.60	5.93	82.8	5.8	28.10	8.00	
						3.190	28.40	5.28	81.3	6.0	29.50	7.80	
						3.212	28.80	5.93	82.8	5.7	29.60	7.90	
2011/9/12 12:25	WY2	ME	828989	810395	7.5	1.004	29.10	6.11	85.5	4.6	29.30	7.90	9
						0.982	29.20	6.12	86.1	4.9	28.80	8.00	
						3.791	27.70	5.72	83.1	4.5	30.10	7.90	13.2
						3.776	27.50	5.65	81.8	4.4	30.40	7.90	
						6.458	27.40	5.69	82.2	5.1	32.10	8.00	
						6.481	27.30	5.58	82.6	5.0	32.20	7.90	
2011/9/12 12:19	WY3	ME	829181	809874	4.4	1.122	29.00	6.22	86.3	5.9	28.60	8.00	8.3
						1.041	28.90	6.37	87.1	5.8	28.80	7.90	
						3.386	28.70	6.14	85.3	5.8	30.10	7.80	8
						3.393	28.60	5.94	81.5	5.9	30.20	7.90	
2011/9/12 12:44	CY1	ME	828384	810828	13.0	1.062	28.80	5.61	84.3	5.2	28.40	7.90	10.6
						1.018	28.90	5.31	82.1	4.9	28.30	8.00	
						6.609	28.10	5.11	80.3	5.2	30.50	8.20	4.8
						6.572	28.10	5.25	81.5	5.2	30.50	8.10	
						12.116	27.40	5.14	80.4	6.2	32.50	8.20	
11.983	27.50	5.11	80.3	6.0	32.40	8.10	2.8						
2011/9/12 11:51	CY2	ME	828011	808829	17.5	1.005	28.10	6.03	85.1	7.1	29.50	7.80	2.6
						0.980	28.30	5.89	84.9	7.2	29.40	7.70	
						8.817	27.10	5.63	82.6	7.3	30.30	7.80	2.6
						8.649	27.00	5.66	82.5	7.0	30.20	7.90	
						16.512	26.50	5.13	80.9	8.1	31.50	7.70	
						16.485	26.50	5.12	80.6	8.3	31.40	7.70	
2011/9/12 17:46	WY1	MF	829158	809577	4.3	1.013	28.80	6.12	86.6	5.1	29.10	7.80	4.3
						0.996	28.50	6.04	84.6	5.6	28.90	7.90	
						3.287	28.10	5.93	83.5	6.0	31.50	7.80	5.6
						3.307	28.10	6.11	86.5	5.9	31.60	7.80	
2011/9/12 18:16	WY2	MF	829001	810398	7.9	1.055	27.80	5.73	82.5	4.2	29.60	7.90	5.4
						0.993	27.80	5.83	83.3	4.6	29.50	8.00	
						4.016	27.50	5.74	82.5	4.7	30.60	8.00	6.2
						3.972	27.50	5.92	84.7	4.6	30.40	7.90	
						6.884	26.90	5.50	81.8	5.0	31.80	7.70	
						6.907	26.90	5.64	83.2	5.2	31.90	7.80	
2011/9/12 18:01	WY3	MF	829218	809869	4.5	1.024	28.20	6.01	85.2	6.0	28.10	7.50	6.1
						1.004	28.20	5.93	84.8	6.3	28.20	7.60	
						3.483	27.20	5.71	83.6	6.0	30.10	7.70	3.3
						3.497	27.30	5.87	83.1	5.9	30.20	7.60	
2011/9/12 18:29	CY1	MF	828397	810811	13.2	1.127	28.30	6.13	86.6	7.2	28.90	8.20	2.2
						1.038	28.50	6.01	85.7	7.1	28.80	8.10	
						6.641	28.10	5.91	83.8	7.6	30.60	8.00	3.9
						6.616	28.10	5.93	83.7	7.4	30.50	8.10	
						12.233	27.20	5.78	82.2	7.9	31.60	8.00	
						12.209	27.20	5.82	83.3	9.1	31.40	7.90	
2011/9/12 17:35	CY2	MF	828001	808818	17.7	1.028	29.20	6.09	85.5	5.9	28.10	7.90	3.7
						0.974	29.20	6.12	87.4	6.3	28.20	7.80	
						8.875	28.60	6.11	87.1	6.6	30.40	7.60	6.8
						8.843	28.60	5.99	84.0	6.8	30.50	7.70	
						16.614	27.80	5.89	81.2	6.1	31.10	7.60	
						16.658	27.80	5.93	83.3	6.3	31.20	7.70	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 15-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2011/9/15 12:53	WY1	ME	829152	809546	4.6	1.002	29.30	7.01	86.2	3.7	31.20	8.00	16.6
						1.023	29.40	6.94	86.0	4.2	28.70	8.00	
						3.655	29.20	6.82	89.7	4.0	30.30	8.12	17.1
						3.625	28.90	6.53	88.3	4.3	30.70	8.10	
2011/9/15 13:21	WY2	ME	829015	810404	7.8	1.026	29.10	7.32	86.5	4.1	27.20	8.40	8.6
						1.055	29.40	7.01	85.1	5.2	28.30	8.34	
						3.890	28.80	6.83	82.3	4.23	30.10	8.00	11.2
						3.912	28.60	6.56	83.8	3.86	30.20	8.10	
						6.860	27.90	6.42	80.1	3.12	26.70	8.20	4.3
						6.840	28.20	6.31	79.4	3.67	27.20	8.23	
2011/9/15 13:06	WY3	ME	829199	809845	4.5	1.025	28.80	7.16	88.4	5.01	31.40	8.10	7.5
						1.022	28.70	6.83	87.2	3.92	32.30	8.15	
						3.564	28.20	6.72	85.1	3.62	29.80	8.32	8.3
						3.546	28.50	6.65	84.7	4.37	25.20	8.30	
2011/9/15 13:37	CY1	ME	828411	810781	11.2	1.054	29.30	6.88	85.6	3.28	29.80	8.10	3.4
						1.064	29.50	6.71	84.1	3.02	29.20	8.15	
						5.610	29.20	6.62	77.4	4.17	30.10	7.90	5.3
						5.601	29.10	6.53	82.6	4.28	30.30	7.85	
						10.231	29.00	6.42	82.3	3.29	27.70	8.40	3.9
						10.220	28.70	6.36	75.2	3.36	27.90	8.35	
2011/9/15 13:58	CY2	ME	828018	808825	17.5	1.011	29.10	7.02	84.2	4.07	29.10	8.30	4.4
						1.003	29.20	6.81	85.1	3.91	29.50	8.22	
						8.750	28.50	6.62	77.6	3.08	30.10	8.20	6.2
						8.765	28.60	6.54	78.3	3.82	30.20	8.15	
						16.546	28.10	6.36	79.5	3.62	31.30	8.00	3.5
						16.550	28.30	6.17	74.9	4.18	31.40	7.99	
2011/9/15 8:31	WY1	MF	829172	809565	4.2	1.022	27.80	6.96	94.2	3.79	33.60	8.10	4.3
						1.031	27.90	6.86	94.1	5.12	30.90	8.12	
						3.211	26.40	6.57	93.1	2.38	31.40	8.10	5
						3.212	26.30	6.56	93.2	2.62	30.20	8.12	
2011/9/15 8:59	WY2	MF	829004	810396	7.1	1.010	28.40	7.04	90.9	4.14	32.40	7.80	6.3
						1.002	28.20	7.02	90.2	4.02	33.80	7.80	
						3.417	27.80	6.92	92.8	3.92	32.80	7.90	3.4
						3.475	27.40	6.82	92.1	3.96	30.90	7.90	
						6.110	26.10	6.72	94.2	3.86	34.20	7.90	4.6
						6.152	26.30	6.82	94.1	3.81	32.90	8.00	
2011/9/15 8:46	WY3	MF	829199	809871	4.7	1.051	28.40	6.92	90.1	4.38	30.30	8.00	2.3
						1.059	28.40	6.94	90.1	4.28	30.60	8.00	
						3.752	26.20	6.56	89.2	4.62	33.60	7.80	4
						3.750	26.10	6.42	89.1	4.28	31.40	7.85	
2011/9/15 9:17	CY1	MF	828411	810818	11.1	1.022	28.30	6.86	93.2	4.42	31.80	8.00	4.2
						1.031	28.10	6.82	93.4	4.26	30.40	8.05	
						5.620	27.80	6.46	92.9	4.07	33.20	8.10	4
						5.611	27.90	6.32	91.6	3.92	30.20	8.10	
						10.164	26.90	6.32	90.9	4.06	33.60	8.40	4.9
						10.120	26.80	6.16	88.8	3.96	30.40	8.40	
2011/9/15 9:39	CY2	MF	828015	808811	17.6	1.005	28.60	7.02	95.3	4.32	30.90	8.40	6.5
						1.025	28.80	7.01	95.2	4.56	32.80	8.40	
						8.822	28.40	6.81	92.8	4.62	34.20	8.20	4.5
						8.825	28.70	6.80	92.1	4.78	31.20	8.20	
						16.550	27.90	6.72	90.2	4.79	34.20	8.00	6.6
						16.640	27.60	6.79	90.1	3.86	30.60	8.00	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 17-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
9/17/2011 14:16:10	WY1	ME	829156	809546	4.3	1.021	29.00	5.29	81.4	3.58	30.40	8.12	7.8
						1.008	29.00	5.23	80.3	3.73	30.40	8.07	
						3.254	28.90	5.30	81.4	2.86	30.60	8.13	
						3.286	28.90	5.32	81.8	2.77	30.60	8.16	
9/17/2011 14:41:07	WY2	ME	829008	840404	7.1	1.005	29.00	5.14	79.0	3.12	30.40	8.11	5.8
						0.979	29.00	5.16	79.4	3.32	30.38	8.26	
						3.648	28.90	5.11	78.6	5.59	30.56	8.16	11.1
						3.675	28.90	5.18	79.5	5.47	30.55	8.15	
						6.082	28.70	5.26	80.9	3.74	30.88	8.07	6.3
						6.097	28.70	5.14	79.0	3.92	30.90	8.06	
9/17/2011 14:29:40	WY3	ME	829195	809843	4.5	1.141	29.00	5.31	81.7	4.73	30.39	8.13	7.3
						1.053	29.00	5.27	81.0	4.78	30.39	8.12	
						3.521	28.80	5.32	81.7	3.59	30.77	8.13	5.8
						3.508	28.80	5.31	81.7	3.79	30.88	8.10	
9/17/2011 14:59:59	CY1	ME	828411	810816	11.9	0.973	29.00	5.28	81.2	2.86	30.12	8.06	4.2
						0.996	29.00	5.26	80.8	2.73	30.08	8.05	
						5.940	28.80	5.31	81.6	5.15	30.56	8.11	5.5
						6.017	28.80	5.01	76.9	5.07	30.66	8.10	
						10.841	28.50	5.16	79.4	4.32	30.89	8.09	6
						10.915	28.50	5.28	81.2	4.29	30.99	8.09	
9/17/2011 13:57:12	CY2	ME	828004	808792	17.3	1.022	29.00	5.26	80.7	6.20	30.00	8.04	6.4
						1.009	29.00	5.35	82.2	6.42	30.03	8.04	
						8.684	28.60	5.32	81.7	3.99	30.38	8.12	4.6
						8.662	28.60	5.28	81.2	4.02	30.39	8.12	
						16.257	28.20	5.33	82.0	7.02	30.68	8.13	8.9
						16.281	28.20	5.32	81.8	7.12	30.69	8.14	
9/17/2011 08:26:02	WY1	MF	829152	809575	4.6	1.117	28.80	5.06	77.3	2.81	29.88	8.02	4.9
						1.062	28.80	4.89	74.8	2.95	29.93	8.00	
						3.581	28.50	4.40	67.1	7.31	30.65	7.98	12.6
						3.604	28.50	4.26	65.0	7.39	30.67	7.95	
9/17/2011 08:45:50	WY2	MF	829001	810392	7.2	1.007	28.70	6.61	100.7	5.22	29.49	8.23	8.9
						1.012	28.70	5.49	83.8	5.26	29.96	8.13	
						3.616	28.60	4.92	75.3	8.56	30.10	8.09	11.4
						3.594	28.60	4.84	74.0	8.79	30.12	8.07	
						6.188	28.50	5.92	90.7	5.73	30.16	8.06	7.6
						6.206	28.50	4.67	71.5	5.97	30.17	8.06	
9/17/2011 08:35:49	WY3	MF	829188	809858	4.3	1.013	29.80	7.13	108.5	9.04	29.45	8.33	11.4
						0.997	28.80	6.75	102.7	9.02	29.01	8.18	
						3.240	28.50	5.14	78.6	4.33	30.05	8.11	7.4
						3.279	28.50	4.78	73.2	4.14	30.06	8.09	
9/17/2011 09:07:45	CY1	MF	828382	810796	12.8	1.112	28.70	5.16	78.7	9.11	29.89	7.99	11.4
						1.004	28.70	5.13	78.3	8.96	29.90	7.99	
						6.408	28.50	5.19	79.6	8.89	30.22	8.07	11.3
						6.372	28.50	5.19	79.5	8.83	30.24	8.08	
						11.785	28.10	4.86	74.5	10.50	30.23	8.09	14.2
						11.916	28.10	5.11	78.3	10.63	30.24	8.08	
9/17/2011 09:49:22	CY2	MF	828016	808791	17.1	1.147	28.90	5.17	79.2	5.14	30.11	8.05	8
						1.033	28.90	5.17	79.1	5.22	30.13	8.05	
						8.572	28.20	5.00	76.5	9.20	30.16	8.03	13.3
						8.549	28.20	4.30	65.9	9.45	30.20	8.05	
						16.084	27.90	4.94	75.6	5.51	30.66	8.06	6.9
						16.021	27.90	5.05	77.2	5.45	30.56	8.04	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 19-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
9/19/2011 15:04:22	WY1	ME	829156	809571	4.3	1.051	28.10	5.64	85.6	2.89	30.97	8.09	6.3
						1.017	28.10	5.58	84.9	2.90	31.04	8.12	
						3.292	27.90	5.56	84.6	5.22	31.10	8.12	
						3.314	27.90	5.43	82.7	5.31	31.10	8.12	
9/19/2011 15:31:46	WY2	ME	829022	810385	7.5	1.058	28.30	5.44	83.0	3.71	30.17	8.12	6.9
						1.014	28.30	5.37	82.0	3.63	30.18	8.12	
						3.781	28.10	5.15	78.6	2.72	31.15	8.12	
						3.766	28.10	5.04	76.9	2.68	31.14	8.09	
						6.519	28.00	4.63	70.6	4.93	31.33	8.12	
						6.483	28.00	4.66	71.1	4.76	31.35	8.12	
9/19/2011 15:16:30	WY3	ME	829220	809836	4.1	1.008	28.20	5.35	81.5	4.02	31.10	8.12	6.2
						0.985	28.20	5.42	82.7	3.86	31.10	8.12	
						3.074	28.00	5.51	84.0	8.04	31.55	8.10	
						3.097	28.00	5.36	81.7	7.91	31.55	8.11	
9/19/2011 15:45:18	CY1	ME	828415	810794	11.8	1.048	28.20	5.44	82.6	4.25	30.63	8.13	7.7
						1.005	28.20	5.46	83.1	4.17	30.55	8.12	
						5.912	28.00	5.52	84.2	6.09	31.12	8.11	
						5.895	28.00	5.37	81.9	5.94	31.13	8.11	
						10.784	27.80	5.14	78.5	7.48	31.56	8.11	
9/19/2011 14:50:07	CY2	ME	828025	808812	17.3	10.811	27.80	4.97	75.8	7.59	31.56	8.12	10.4
						1.138	28.10	5.49	83.5	5.81	30.88	8.11	
						1.034	28.10	5.54	84.3	6.11	30.97	8.11	
						8.664	27.90	5.51	83.9	7.37	31.11	8.11	
						8.631	27.90	5.42	82.7	7.28	31.11	8.11	
9/19/2011 10:06:01	WY1	MF	829178	809576	4.2	16.288	27.50	5.31	80.9	8.36	31.56	8.11	8.5
						16.305	27.50	5.24	79.9	8.10	31.64	8.12	
						1.122	28.90	5.52	81.1	7.94	29.35	8.10	
						1.051	28.90	5.11	78.0	7.88	29.34	8.02	
9/19/2011 10:26:02	WY2	MF	829012	810398	7.1	3.219	28.50	4.68	71.5	7.26	29.89	7.97	8.4
						3.185	28.50	4.35	66.5	7.39	29.89	7.95	
						1.086	29.20	6.38	92.7	4.91	29.53	8.28	
						1.047	29.00	6.15	94.1	4.75	29.53	8.10	
						3.562	28.50	5.18	79.2	5.78	29.77	7.99	
9/19/2011 10:15:18	WY3	MF	829196	809862	4.3	3.547	28.50	5.00	76.4	5.85	29.77	7.98	7.1
						6.084	28.10	5.08	77.4	4.83	30.45	7.99	
						6.111	28.10	5.06	77.2	4.61	30.55	7.97	
						1.072	28.80	5.84	89.0	5.63	29.42	8.10	
						1.043	28.80	5.26	80.4	5.49	29.87	8.04	
						3.275	28.50	4.88	74.5	11.00	29.94	8.02	
9/19/2011 10:37:43	CY1	MF	828389	810811	11.7	3.294	28.50	4.82	73.5	10.79	29.94	7.98	14.2
						1.011	28.50	4.85	74.3	8.44	30.55	8.13	
						0.985	28.50	4.74	72.7	8.17	30.46	8.12	
						5.764	28.10	4.79	73.5	8.77	31.12	8.12	
						5.819	28.10	4.72	72.3	8.91	31.12	8.12	
						10.682	27.80	4.72	72.3	4.84	31.64	8.12	
9/19/2011 10:53:53	CY2	MF	828012	808816	17.2	10.689	27.80	4.76	73.0	4.77	31.57	8.13	8.6
						1.043	28.60	4.62	70.9	4.31	30.31	8.12	
						0.994	28.60	4.68	71.7	4.20	30.33	8.12	
						8.618	28.20	4.62	70.8	6.23	31.12	8.12	
						8.583	28.20	4.57	70.0	6.11	31.13	8.12	
						16.179	27.50	4.67	71.7	6.87	31.56	8.12	
16.192	27.50	4.66	71.4	7.04	31.55	8.12							

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 21-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
9/21/2011 08:19:02	WY1	ME	8291523	809564	4.6	1.031	28.90	5.84	89.8	5.13	30.73	8.13	9
						0.995	28.80	5.80	89.1	5.30	30.77	8.11	
						3.584	28.70	5.41	83.0	3.30	30.90	8.11	
						3.605	28.70	5.35	82.2	3.20	31.13	8.08	
9/21/2011 08:51:20	WY2	ME	829016	810392	7.3	1.072	28.90	5.74	88.3	4.39	30.77	8.13	7.8
						1.024	28.80	5.59	85.9	4.46	30.80	8.11	
						3.681	28.70	5.48	84.1	5.08	30.95	8.12	10.1
						3.665	28.70	5.23	80.3	4.97	31.04	8.08	
						6.291	28.30	5.18	79.7	3.92	31.34	8.12	6.6
						6.312	28.30	4.96	76.4	4.11	31.36	8.14	
9/21/2011 08:37:14	WY3	ME	829211	809834	4.4	1.211	28.90	5.82	89.5	6.86	30.60	8.14	10.6
						1.069	28.90	5.86	90.2	6.94	30.66	8.13	
						3.417	28.70	5.82	89.6	7.97	30.78	8.08	12.4
						3.394	28.70	5.45	83.6	8.10	30.91	8.11	
9/21/2011 09:14:54	CY1	ME	828416	810813	11.8	1.028	28.80	5.58	85.6	7.13	30.70	8.12	7.8
						0.989	28.80	5.53	84.9	7.07	30.78	8.11	
						5.907	28.70	5.52	84.8	7.20	31.09	8.17	7.8
						5.886	28.70	5.52	84.8	7.18	31.19	8.14	
						10.812	28.20	5.00	76.9	6.11	31.23	8.15	7.1
						10.793	28.20	5.07	78.0	6.07	31.24	8.13	
9/21/2011 08:03:43	CY2	ME	808015	808826	17.8	1.010	28.80	5.59	85.9	7.65	30.75	8.11	7.9
						0.984	28.80	5.55	85.3	7.92	30.78	8.11	
						8.922	28.20	5.67	87.1	5.55	30.87	8.12	6.4
						8.907	28.20	5.38	82.7	5.60	31.04	8.12	
						16.775	27.90	5.17	79.5	3.79	31.27	8.15	4.8
						16.792	27.90	5.11	78.7	3.90	31.32	8.16	
9/21/2011 17:11:38	WY1	MF	829192	809565	4.5	1.004	29.00	5.24	80.8	4.35	30.81	8.06	7.4
						1.013	29.00	5.37	82.8	4.46	30.86	8.06	
						3.517	28.80	5.79	88.9	4.53	30.69	8.11	7.5
						3.502	28.80	5.53	85.0	4.40	30.79	8.11	
9/21/2011 17:38:44	WY2	MF	829006	810422	7.4	1.063	28.90	6.12	94.2	5.52	30.73	8.20	9.4
						1.014	28.90	6.08	93.6	5.56	30.78	8.17	
						3.714	28.80	5.93	91.2	10.76	30.77	8.15	13.8
						3.689	28.80	5.60	85.9	10.97	30.87	8.13	
						6.425	28.20	5.48	84.2	8.45	31.05	8.12	11.2
						6.407	28.20	5.30	81.5	8.80	31.16	8.13	
9/21/2011 17:04:49	WY3	MF	829213	809878	4.3	1.029	29.00	5.45	84.1	6.50	30.87	8.04	8.2
						0.996	28.90	5.31	81.9	6.49	30.94	8.02	
						3.315	28.60	5.78	88.7	5.57	31.02	8.12	6.1
						3.308	28.60	5.64	86.7	5.41	30.11	8.11	
9/21/2011 17:51:54	CY1	MF	828395	810814	11.3	1.006	28.80	5.56	85.6	8.44	30.72	8.10	8.1
						1.012	28.70	5.50	84.3	8.29	30.71	8.12	
						5.661	28.50	5.50	84.4	5.43	30.81	8.12	6.9
						5.648	28.50	5.55	85.1	5.39	30.92	8.30	
						10.293	28.10	5.28	81.3	3.11	31.22	8.14	4.2
						10.317	28.10	5.21	80.2	3.15	31.30	8.14	
9/21/2011 17:20:16	CY2	MF	828022	808785	17.3	1.004	28.60	5.42	83.1	4.97	30.95	8.08	6.4
						0.977	28.60	5.47	83.9	5.12	30.86	8.10	
						8.629	28.40	5.35	82.2	4.12	31.12	8.12	5.9
						8.641	28.40	5.19	79.7	4.26	31.17	8.12	
						16.281	28.10	4.91	75.5	6.95	31.32	8.13	8.7
						16.303	28.10	5.00	76.9	6.87	31.31	8.13	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 23-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
9/23/2011 08:25:39	WY1	ME	829152	809561	4.3	1.027	28.20	5.70	86.9	5.95	31.09	8.14	13.4
						0.997	28.20	5.59	85.2	6.15	31.14	8.14	
						3.284	28.10	5.65	86.2	7.45	31.27	8.16	
						3.315	28.10	5.63	86.1	7.45	31.26	8.16	
9/23/2011 08:43:31	WY2	ME	828984	810387	7.3	1.016	28.40	5.34	81.8	3.15	30.88	8.15	6.0
						0.981	28.40	5.38	82.5	3.39	30.88	8.14	
						3.662	28.20	5.65	86.5	2.35	31.34	8.20	
						3.648	28.20	5.40	82.7	2.27	31.34	8.16	
						6.221	28.00	5.10	78.1	5.82	31.68	8.13	
						6.194	28.00	4.97	76.0	6.00	31.71	8.13	
9/23/2011 08:32:41	WY3	ME	829191	809871	4.5	1.026	28.40	5.66	86.5	4.59	31.27	8.16	6.9
						1.004	28.40	5.68	86.9	4.39	31.28	8.16	
						3.522	28.10	5.73	87.6	4.53	31.56	8.17	
						3.507	28.10	5.66	86.7	4.68	31.66	8.17	
9/23/2011 08:59:50	CY1	ME	828421	810813	11.3	1.006	28.20	5.41	82.4	3.77	31.08	8.10	5.6
						1.013	28.20	5.42	82.4	3.64	31.08	8.11	
						5.672	28.00	5.55	84.6	5.78	31.25	8.08	
						5.647	28.00	5.48	83.6	5.74	31.26	8.12	
						10.284	27.80	5.58	85.2	5.35	31.55	8.13	
10.309	27.80	5.52	84.3	5.34	31.46	8.13							
9/23/2011 09:24:29	CY2	ME	808004	808818	17.1	0.992	28.20	5.60	85.3	8.14	31.10	8.13	7.2
						1.015	28.20	5.47	83.4	8.34	31.13	8.13	
						8.573	27.90	5.31	80.9	7.91	31.56	8.12	
						8.559	27.90	5.48	83.5	8.02	31.56	8.13	
						16.057	27.50	5.05	77.1	5.08	31.89	8.11	
						16.083	27.50	5.02	76.5	5.19	31.87	8.09	
9/23/2011 16:17:40	WY1	MF	829164	809572	4.4	1.006	28.40	5.55	84.9	6.36	31.28	8.15	7.8
						1.013	28.40	5.64	86.3	6.88	31.29	8.16	
						3.419	28.20	5.37	82.2	6.06	31.64	8.03	
						3.385	28.20	5.23	79.9	6.10	31.68	8.10	
9/23/2011 16:47:05	WY2	MF	829023	810385	7.2	1.041	28.40	5.56	85.0	6.03	31.29	8.15	9.3
						1.016	28.40	5.57	85.2	6.09	31.28	8.15	
						3.624	28.10	5.61	85.8	6.03	31.64	8.20	
						3.605	28.10	5.74	87.3	6.12	31.55	8.14	
						6.218	27.90	5.36	81.9	6.70	31.98	8.14	
						6.184	27.90	5.24	80.1	6.82	31.99	8.15	
9/23/2011 16:29:50	WY3	MF	829219	809834	4.5	1.001	28.40	5.41	82.7	8.81	31.27	8.22	9.8
						1.014	28.40	5.56	85.0	8.82	31.28	8.18	
						3.528	28.20	5.68	86.8	9.83	31.56	8.14	
						3.505	28.20	5.60	85.7	9.52	31.65	8.15	
						1.147	28.30	5.38	82.1	8.42	30.89	8.13	
9/23/2011 17:05:02	CY1	MF	828420	810784	11.9	1.053	28.30	5.34	81.4	8.22	30.95	8.15	7.6
						5.977	28.10	5.61	85.7	8.21	31.20	8.13	
						5.942	28.10	5.59	85.4	8.16	31.21	8.14	
						10.877	27.80	5.59	85.4	7.97	31.68	8.13	
						10.903	27.80	5.60	85.5	8.28	31.66	8.16	
						1.021	28.20	5.65	86.1	5.90	30.65	8.13	
9/23/2011 16:03:58	CY2	MF	828005	808818	17.3	1.009	28.20	5.55	84.7	6.10	30.55	8.14	7.5
						8.662	27.90	5.69	86.8	9.42	31.20	8.17	
						8.648	27.90	5.54	84.7	9.61	31.23	8.15	
						16.281	27.50	5.54	84.7	6.14	31.48	8.19	
						16.295	27.50	5.56	85.1	5.98	31.56	8.16	
						16.295	27.50	5.56	85.1	5.98	31.56	8.16	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 26-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
9/26/2011 11:20:11	WY1	ME	829160	809568	4.6	1.084	27.90	5.76	87.6	6.7	31.40	8.13	15.2
						1.035	27.90	5.78	87.7	7.0	31.41	8.15	
						3.617	27.70	5.67	86.2	5.4	31.66	8.15	12.4
						3.639	27.80	5.57	84.6	5.4	31.62	8.15	
9/26/2011 11:42:05	WY2	ME	829017	810417	7.4	1.085	27.90	5.56	84.4	7.7	31.35	8.21	14.7
						1.020	27.90	5.56	84.5	8.3	31.36	8.20	
						3.780	27.70	5.62	85.3	3.1	31.55	8.21	7.1
						3.700	27.70	5.62	85.4	3.0	31.56	8.19	
						6.506	27.60	5.29	80.3	6.0	31.80	8.15	9.4
						6.454	27.60	5.35	81.4	6.2	31.89	8.13	
9/26/2011 11:32:34	WY3	ME	829268	810108	4.5	1.049	27.90	5.83	88.4	3.3	31.20	8.28	5
						0.986	27.90	5.53	84.0	3.2	31.34	8.22	
						3.518	27.80	5.50	83.4	4.1	31.56	8.18	6.7
						3.476	27.80	5.36	81.3	4.2	31.60	8.17	
9/26/2011 12:01:20	CY1	ME	828402	628561	12.2	1.012	27.90	6.24	94.7	10.0	31.25	8.31	14.9
						0.995	27.90	5.99	90.9	9.7	31.28	8.24	
						6.116	27.80	5.87	89.1	18.4	31.65	8.23	19.8
						6.156	27.80	5.86	88.9	18.3	31.65	8.22	
						11.272	27.50	5.84	88.6	12.4	31.87	8.21	13.7
11.267	27.50	5.80	87.9	12.4	31.79	8.21							
9/26/2011 12:15:30	CY2	ME	828019	808798	17.4	1.103	27.90	5.85	88.8	14.5	31.25	8.19	12.8
						1.004	27.90	5.83	88.5	14.8	31.30	8.19	
						8.729	27.50	5.83	88.4	13.4	31.56	8.21	13.9
						8.733	27.50	5.79	87.8	13.6	31.64	8.19	
						16.448	27.20	5.83	88.4	10.1	31.87	8.18	10.3
						16.448	27.20	5.85	88.7	10.3	31.88	8.18	
9/26/2011 16:21:29	WY1	MF	829164	809555.3	4.5	1.052	27.90	5.86	88.9	8.9	31.13	8.17	10.9
						1.008	27.90	5.79	87.8	9.6	31.15	8.19	
						3.670	27.60	5.76	87.3	6.6	31.56	8.18	9.3
						3.670	27.60	5.77	87.5	6.6	31.55	8.18	
9/26/2011 16:51:17	WY2	MF	829002	810403	7.6	1.026	27.80	5.85	88.8	9.0	30.95	8.19	13.9
						0.996	27.90	5.83	88.3	9.1	30.95	8.17	
						3.793	27.60	5.79	87.8	5.2	31.30	8.17	6.5
						3.752	27.60	5.71	86.8	5.2	31.31	8.17	
						6.548	27.20	5.77	87.6	11.3	31.80	8.16	13.5
						6.541	27.20	5.79	87.7	11.5	31.75	8.16	
9/26/2011 16:39:49	WY3	MF	829205	809868	4.5	1.027	27.90	5.78	87.5	11.4	31.18	8.17	12.7
						1.005	27.90	5.79	87.8	11.4	31.30	8.14	
						3.561	27.80	5.86	88.9	10.3	31.65	8.16	11.4
						3.566	27.80	5.84	88.5	10.0	31.55	8.16	
9/26/2011 17:25:53	CY1	MF	828404	810805	12.5	1.066	27.90	5.54	84.3	14.3	31.11	8.20	12.9
						1.013	27.90	5.48	83.3	14.0	31.12	8.19	
						6.332	27.80	5.71	86.6	13.8	31.45	8.19	13.8
						6.343	27.80	5.66	86.0	13.7	31.47	8.19	
						11.591	27.50	5.27	80.2	16.6	31.80	8.18	19.8
11.630	27.50	5.31	80.6	17.3	31.74	8.18							
9/26/2011 17:10:00	CY2	MF	828010	808808	17.3	1.080	27.80	5.89	89.3	9.9	30.97	8.16	12.6
						1.006	27.80	5.86	88.7	10.2	30.95	8.15	
						8.596	27.50	5.87	89.0	10.8	31.29	8.14	13.3
						8.550	27.50	5.84	88.5	11.0	31.29	8.16	
						16.392	27.20	5.39	81.6	11.8	31.65	8.17	13.4
						16.270	27.20	5.45	82.6	11.5	31.55	8.18	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 28-Sep-11

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
9/28/2011 11:50:03	WY1	ME	829159	809570	4.5	1.093	28.50	5.72	87.7	4.35	31.29	8.02	13.1
						1.029	28.50	5.69	87.2	4.50	31.28	8.03	
						3.577	28.30	5.69	87.0	3.23	31.56	8.04	8.9
						3.618	28.30	5.54	84.7	3.22	31.64	8.04	
9/28/2011 12:15:32	WY2	ME	829022	810406	7.5	1.108	28.20	5.57	85.0	6.13	31.36	8.08	6.2
						1.019	28.20	5.61	85.5	6.61	31.37	8.08	
						3.749	28.40	5.69	85.1	2.43	31.55	8.09	8.3
						3.687	28.40	5.68	87.0	2.36	31.65	8.10	
						6.478	28.40	5.71	87.3	3.14	31.89	8.11	7.9
						6.453	28.40	5.65	86.5	3.23	31.90	8.11	
9/28/2011 12:40:32	WY3	ME	829262	810097	4.5	1.079	28.10	5.80	88.4	4.06	31.37	8.17	11.5
						1.006	28.10	5.72	87.1	3.88	31.39	8.13	
						3.615	28.40	5.70	87.1	2.94	31.67	8.13	12.6
						3.627	28.40	5.63	86.1	3.04	31.75	8.13	
9/28/2011 12:52:10	CY1	ME	828396	810814	12.4	1.040	28.00	5.68	86.5	6.33	31.41	8.15	8.7
						0.991	28.00	5.65	86.0	6.11	31.40	8.15	
						6.075	28.60	5.54	85.0	6.34	31.64	8.16	10.9
						6.071	28.60	5.52	84.6	6.30	31.66	8.13	
						11.166	28.30	5.50	84.0	6.62	31.80	8.11	8
						11.146	28.20	5.34	81.6	6.61	31.90	8.14	
9/28/2011 13:20:20	CY2	ME	828017	808799	17.4	1.107	28.20	5.56	84.8	9.27	31.19	8.14	11.3
						1.024	28.20	5.50	83.8	9.49	31.19	8.12	
						8.657	28.60	5.96	91.0	10.51	31.32	8.22	8.2
						8.665	28.60	5.78	88.4	10.66	31.35	8.18	
						16.312	28.30	5.61	85.8	7.13	31.80	8.17	6.8
						16.333	28.20	5.56	84.9	7.28	31.75	8.16	
9/28/2011 17:02:32	WY1	MF	829158	809549	4.5	1.058	28.20	5.51	84.1	8.07	31.16	8.15	8
						1.010	28.20	5.58	85.2	8.73	31.19	8.10	
						3.559	28.20	5.56	84.7	4.44	31.30	8.12	8
						3.559	28.20	5.57	84.9	4.47	31.30	8.13	
9/28/2011 17:10:51	WY2	MF	829002	810401	7.7	1.030	28.20	5.47	83.5	5.77	31.20	8.12	9.3
						0.991	28.20	5.53	84.4	5.83	31.20	8.20	
						3.844	28.20	5.46	83.2	5.16	31.55	8.14	8.1
						3.834	28.20	5.44	82.9	5.23	31.56	8.12	
						6.711	28.20	5.61	85.5	4.44	31.78	8.16	9.6
						6.706	28.20	5.60	85.3	4.52	31.88	8.13	
9/28/2011 17:23:15	WY3	MF	829194	809869	4.4	1.042	28.20	5.60	85.3	6.47	31.23	8.13	7.7
						1.002	28.20	5.56	84.7	6.48	31.20	8.11	
						3.347	28.20	5.62	85.7	9.38	31.50	8.18	10.9
						3.623	28.20	5.55	84.6	9.09	31.46	8.13	
9/28/2011 17:40:14	CY1	MF	828401	810804	12.7	1.058	28.10	6.03	92.0	13.18	31.14	8.14	7.4
						1.007	28.20	5.92	90.5	12.87	31.17	8.13	
						6.303	28.20	5.64	86.0	8.31	31.56	8.13	9.6
						6.288	28.20	5.52	84.2	8.25	31.45	8.13	
						11.552	28.20	5.56	84.8	8.22	31.80	8.14	7.5
						11.598	28.20	5.50	83.8	8.54	31.79	8.12	
9/28/2011 17:57:24	CY2	MF	828007	808805	17.3	1.083	28.10	5.72	87.2	4.88	31.23	8.15	8
						1.005	28.20	5.67	86.4	5.04	31.25	8.13	
						8.634	28.40	5.69	86.8	4.31	31.50	8.16	5.5
						8.661	28.40	5.60	85.5	4.39	31.55	8.14	
						16.304	28.30	5.57	85.0	2.99	31.79	8.15	8.5
						16.330	28.20	5.49	83.7	2.91	31.81	8.14	

Remarks: MF - Middle Flood tide
 ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 30-Sep-11


Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
9/30/2011 14:12:58	WY1	ME	829162	809565	4.5	1.066	28.00	5.41	82.2	4.19	31.20	8.13	3.4
						1.026	28.00	5.44	82.6	4.25	31.20	8.09	
						3.509	27.80	5.55	84.1	4.07	31.50	8.11	
						3.502	27.70	5.48	82.9	3.88	31.56	8.13	
9/30/2011 14:34:51	WY2	ME	829014	810408	7.4	1.073	28.20	5.57	84.6	3.86	31.25	8.08	10.7
						1.020	28.20	5.50	83.7	4.01	31.21	8.12	
						3.772	27.80	5.51	83.5	4.40	31.45	8.12	
						3.715	27.80	5.47	82.9	4.52	31.40	8.12	
						6.473	27.50	5.37	81.4	4.16	31.75	8.13	
						6.438	27.50	5.42	82.2	4.23	31.80	8.13	
9/30/2011 14:23:02	WY3	ME	829279	810176	4.2	1.037	27.70	5.48	82.9	3.94	31.26	8.14	7.2
						0.987	27.70	5.40	81.7	3.86	31.26	8.13	
						3.299	27.50	5.47	82.7	4.11	31.68	8.15	
						3.246	27.50	5.51	83.2	4.24	31.72	8.13	
9/30/2011 14:53:53	CY1	ME	828411	810821	12.6	1.005	28.00	5.48	83.3	4.18	31.22	8.13	9.9
						0.991	28.00	5.48	83.3	4.21	31.21	8.12	
						6.333	27.60	5.59	84.8	4.36	31.36	8.12	
						6.316	27.60	5.45	82.6	4.40	31.55	8.12	
						11.623	27.50	5.35	80.9	4.89	31.80	8.21	
						11.630	27.50	5.19	78.5	4.73	31.80	8.13	
9/30/2011 14:01:31	CY2	ME	828020	808811	17.5	1.064	28.20	5.45	83.0	4.33	31.17	8.14	15
						0.995	28.20	5.50	83.8	4.42	31.18	8.13	
						8.775	28.00	5.54	84.2	4.60	31.60	8.14	
						8.773	28.00	5.41	82.2	4.47	31.60	8.13	
						16.546	27.90	5.41	82.2	4.92	31.98	8.12	
						16.309	27.90	5.42	82.3	5.08	31.89	8.12	
9/30/2011 08:17:16	WY1	MF	829162	809553	4.4	1.026	28.00	5.74	87.2	4.21	31.15	8.16	13.5
						0.992	28.00	5.53	84.0	4.08	31.16	8.11	
						3.452	27.80	5.60	84.8	4.63	31.56	8.17	
						3.428	27.80	5.43	82.2	4.34	31.46	8.08	
9/30/2011 08:32:08	WY2	MF	828993	810414	7.6	1.037	27.80	5.52	83.6	3.90	31.16	8.10	9.1
						1.001	27.80	5.41	82.0	4.12	31.22	8.11	
						3.815	27.50	5.49	83.2	4.35	31.55	8.12	
						3.798	27.50	5.37	81.3	4.27	31.42	8.11	
						6.591	27.20	5.14	77.7	4.06	31.69	8.13	
						6.649	27.20	5.22	78.9	3.89	31.68	8.12	
9/30/2011 08:23:51	WY3	MF	829196	809875	4.6	1.052	28.00	5.85	88.9	3.61	27.35	8.02	8.4
						1.016	28.00	5.66	86.0	3.82	31.02	8.05	
						3.629	27.80	5.32	80.7	4.19	31.56	8.06	
						3.636	27.80	5.22	79.3	4.07	31.49	8.07	
9/30/2011 09:00:25	CY1	MF	828416	810811	12.6	1.061	28.00	5.64	85.7	4.17	31.20	8.18	14.6
						1.011	28.00	5.59	84.9	4.05	31.20	8.16	
						6.386	27.80	5.60	85.0	4.65	31.60	8.15	
						6.379	27.80	5.58	84.7	4.81	31.50	8.15	
						11.683	27.50	5.24	79.2	4.90	31.98	8.18	
						11.616	27.50	5.17	78.3	4.88	31.88	8.16	
9/30/2011 09:19:11	CY2	MF	828018	808811	17.2	1.036	28.10	5.54	84.3	4.36	31.11	8.11	15.3
						0.986	28.10	5.51	83.8	4.29	31.15	8.12	
						8.666	27.70	5.54	83.9	4.98	31.50	8.12	
						8.580	27.70	5.48	82.9	4.73	31.46	8.13	
						16.400	27.30	5.36	81.1	5.04	31.87	8.13	
						16.282	27.30	5.28	79.9	5.11	31.88	8.17	

Remarks: MF - Middle Flood tide
 ME - Middle Ebb tide



Appendix H

Graphical Plots of Monitoring Results


1-hour TSP Monitoring

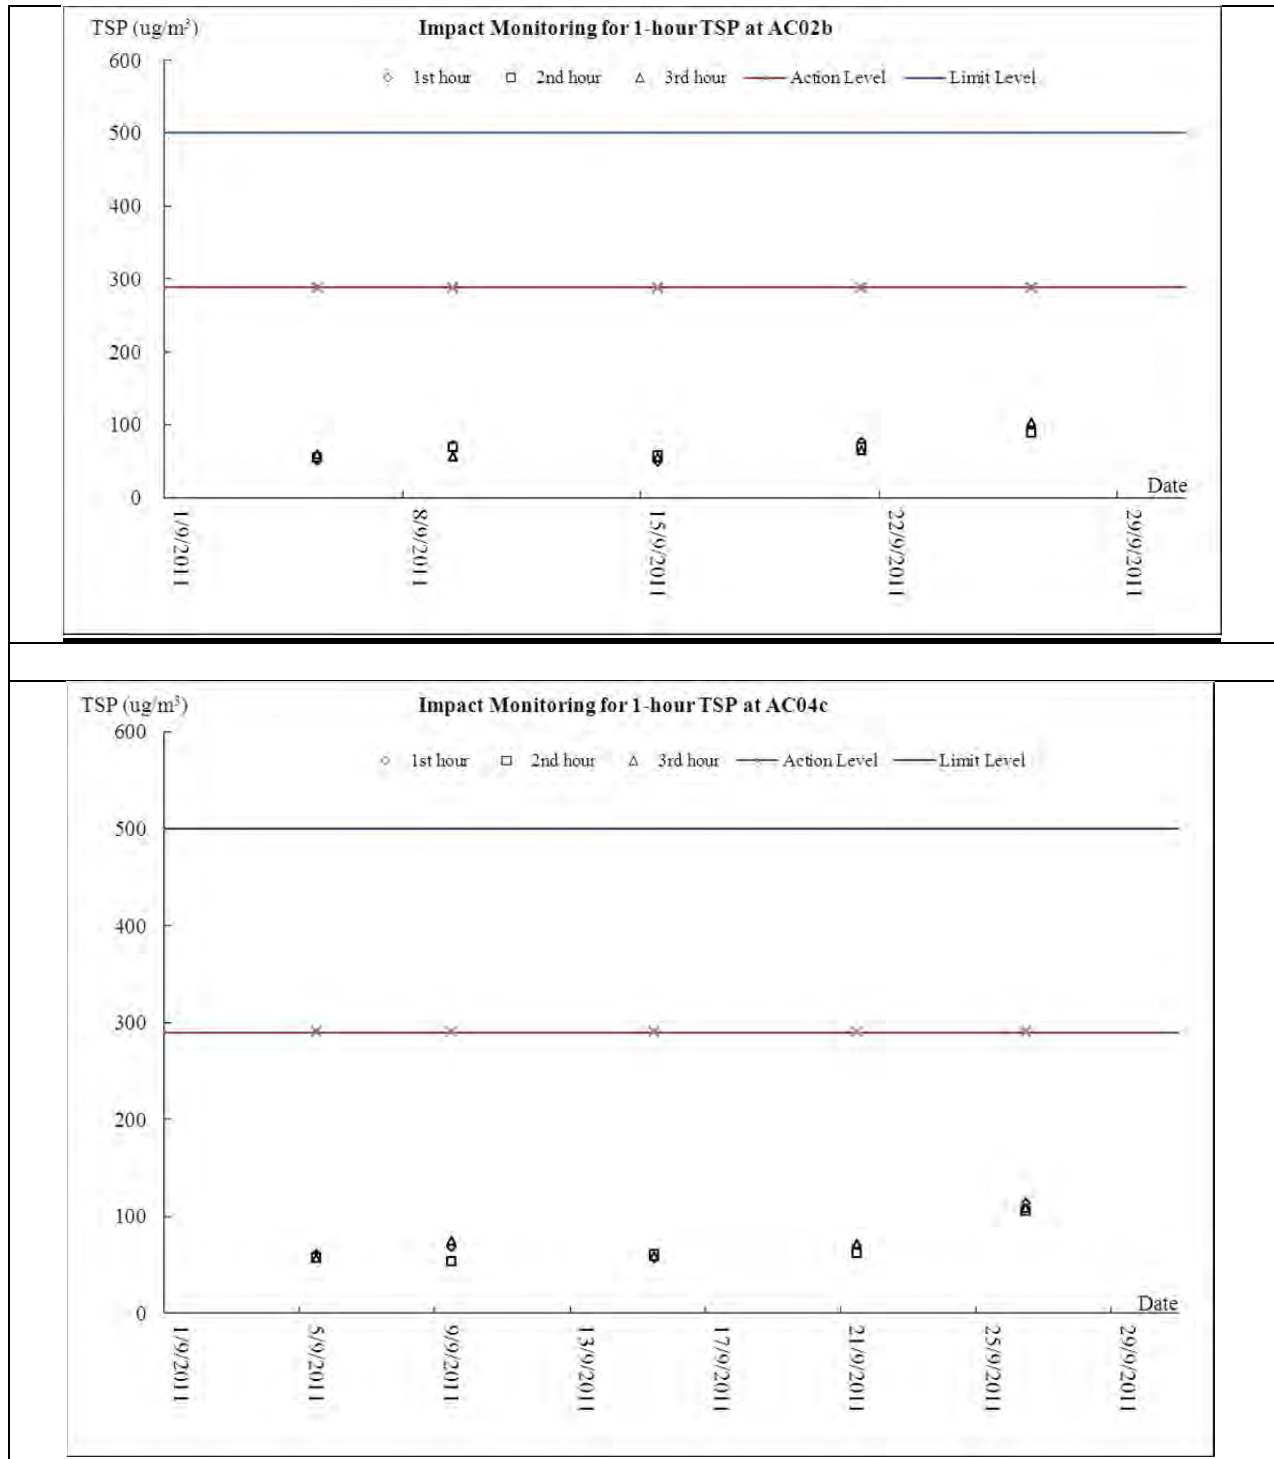



24-hour TSP Monitoring

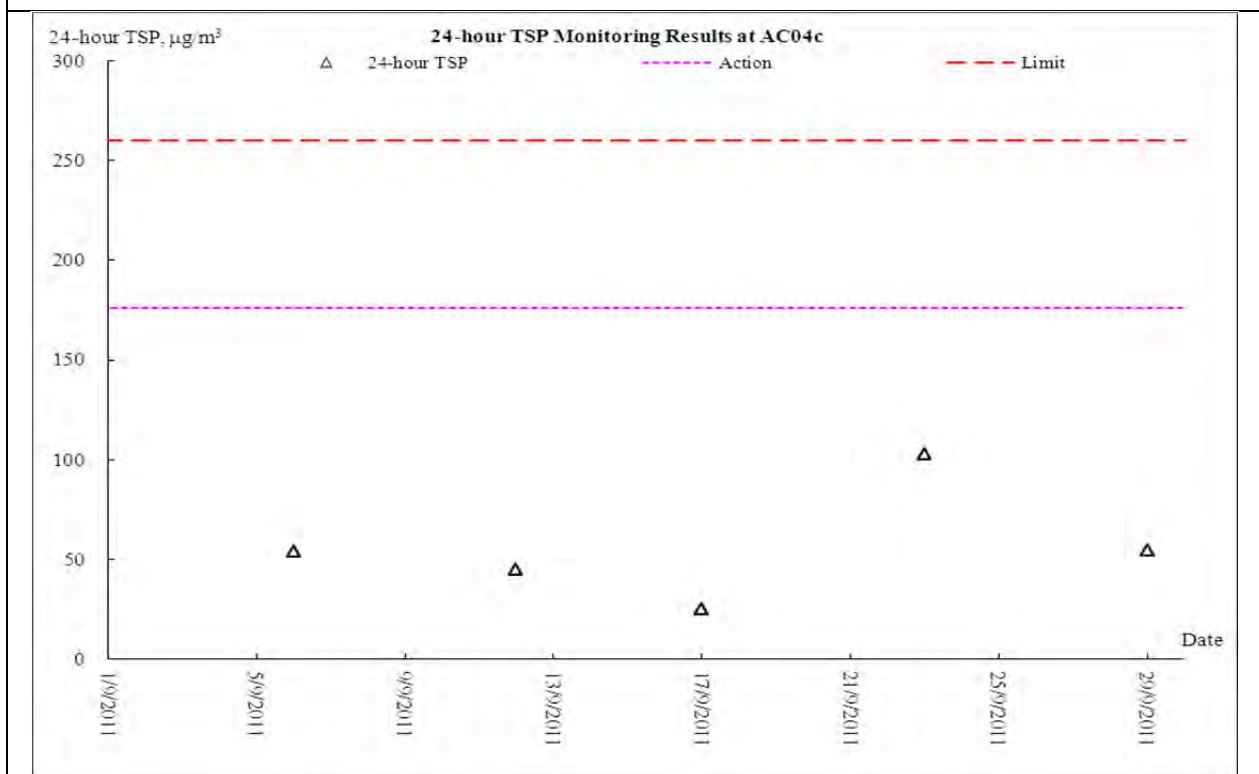
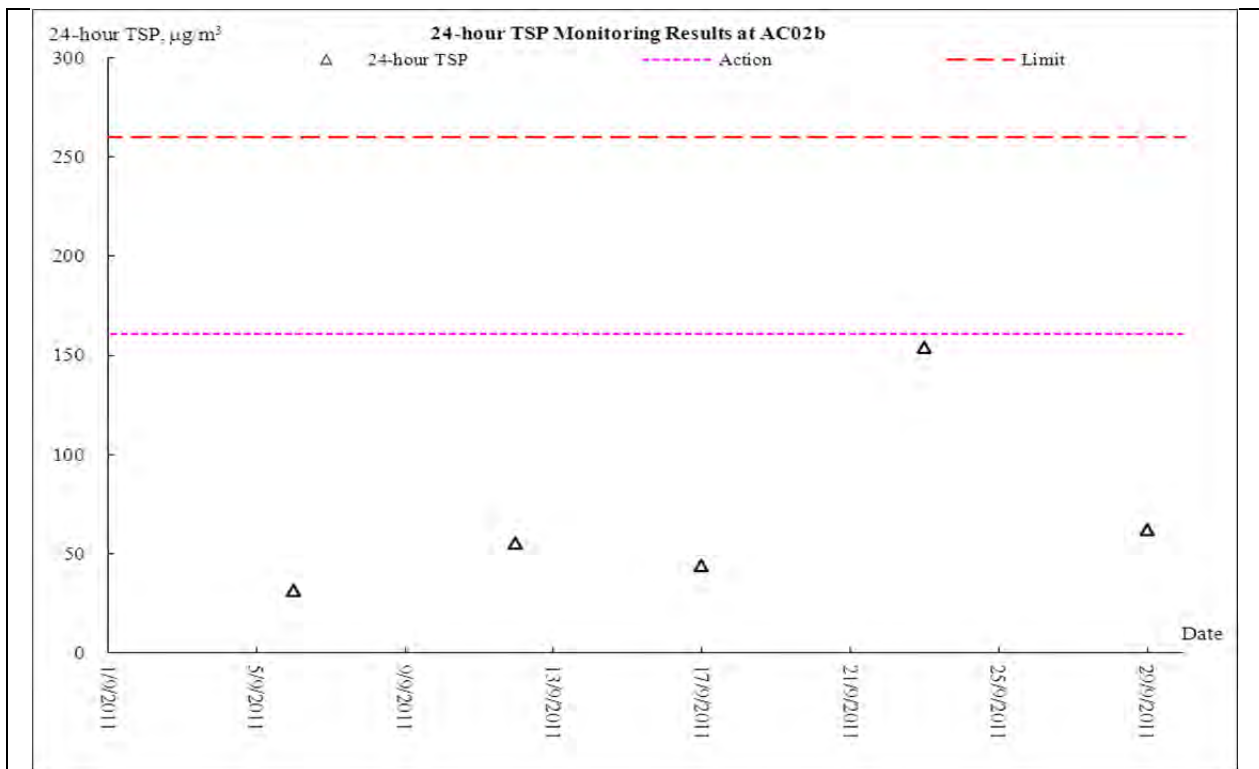


Noise Monitoring


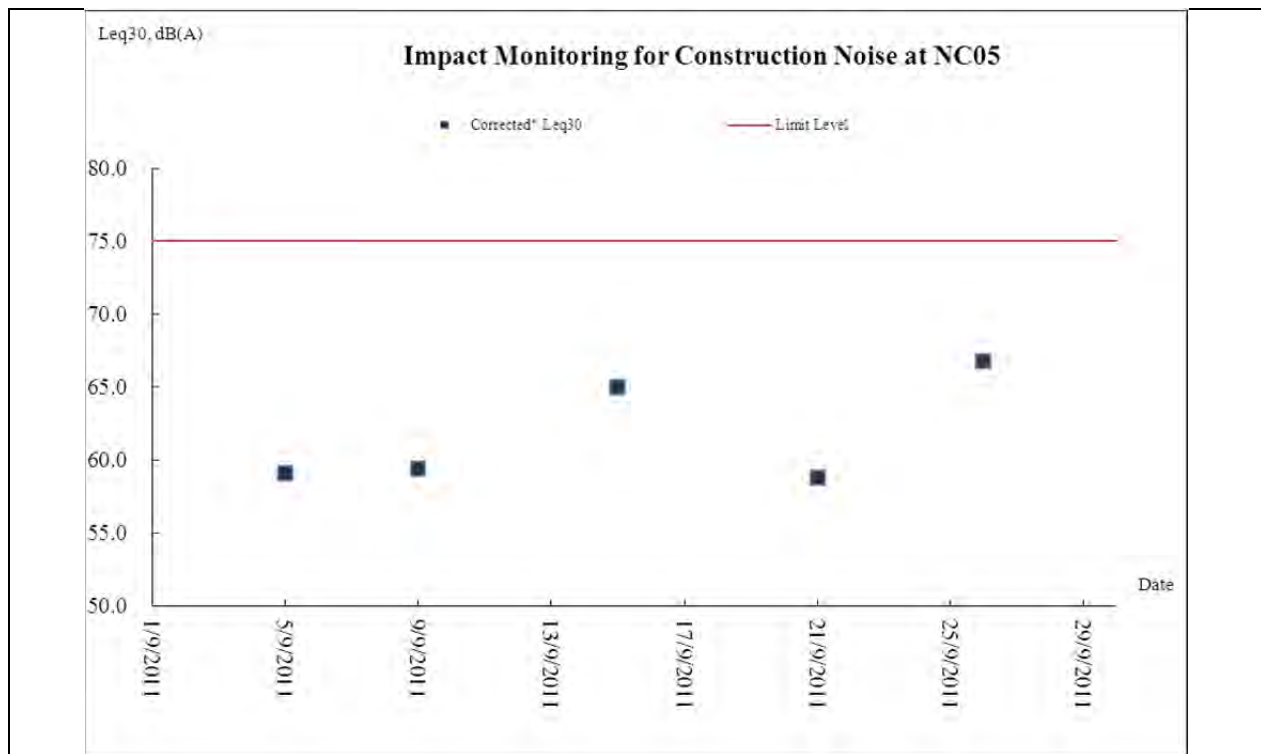




Marine Water Quality Monitoring – Mid Ebb Tide

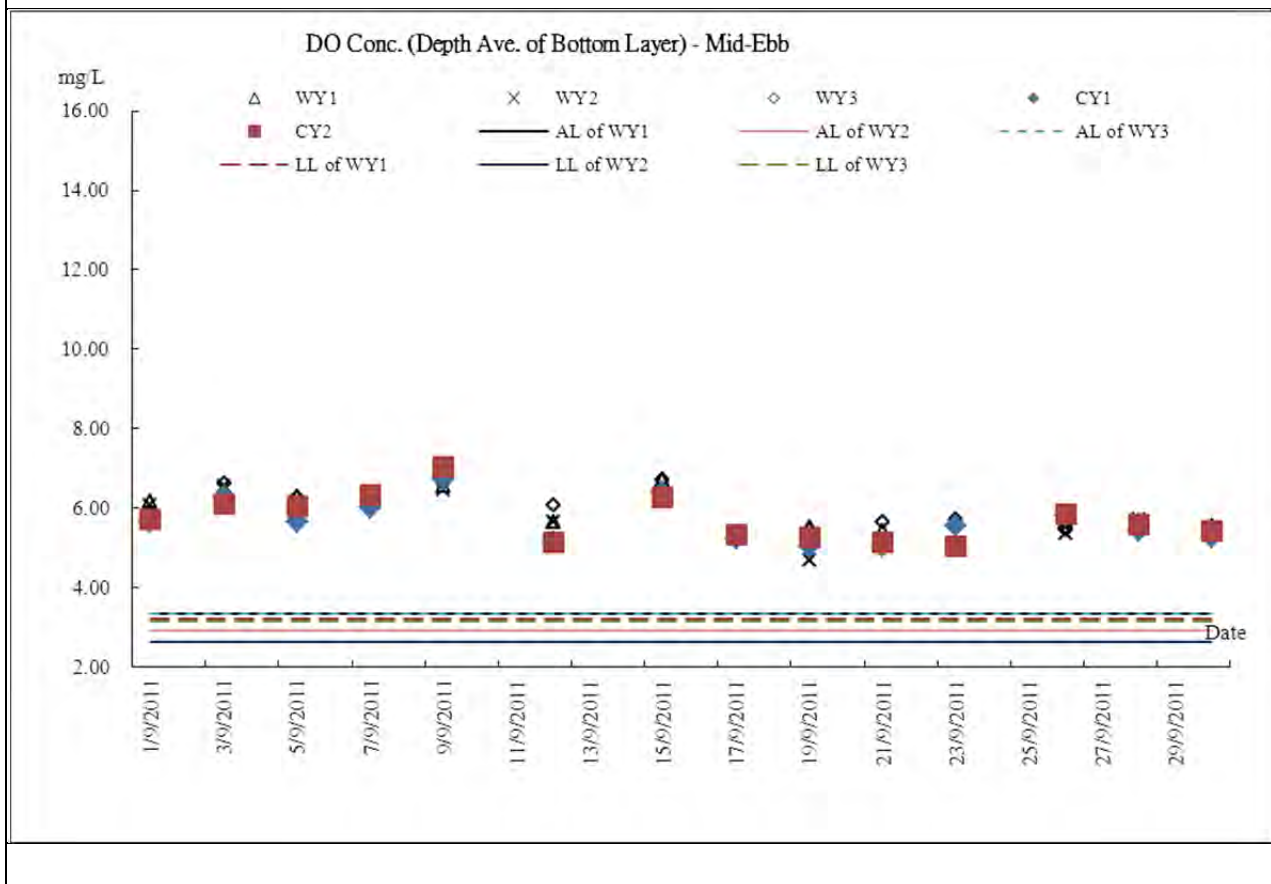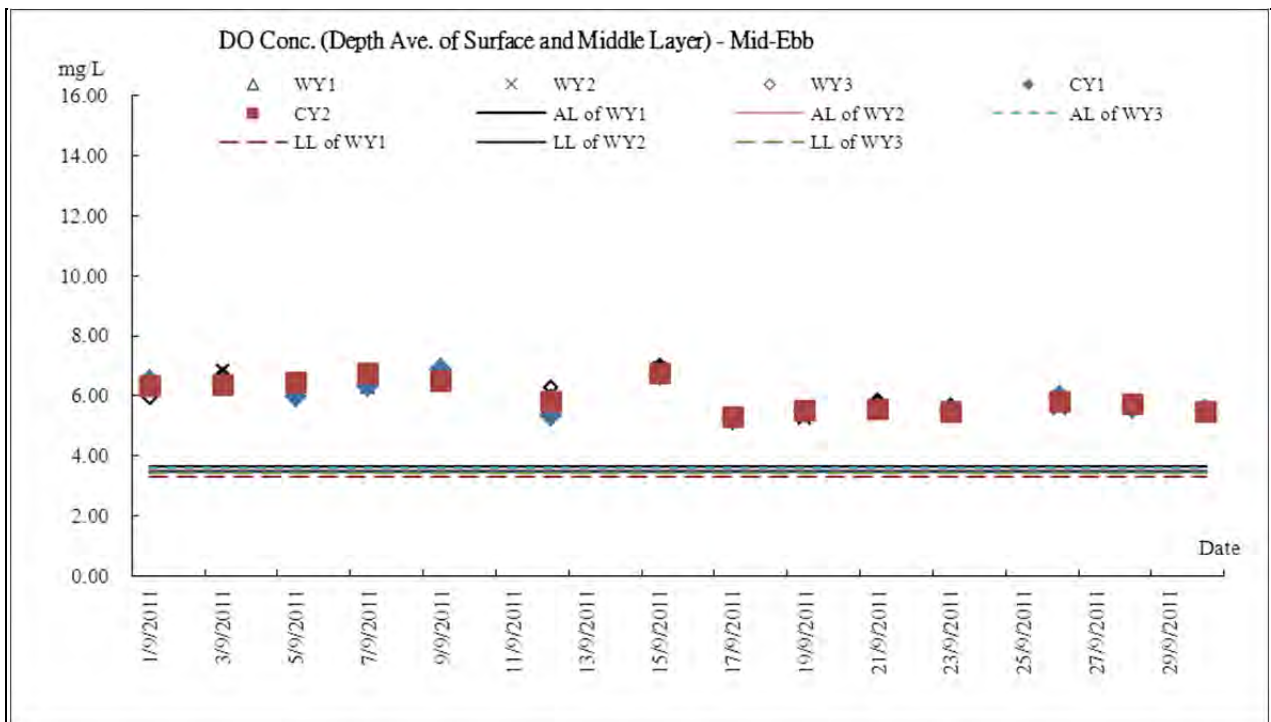

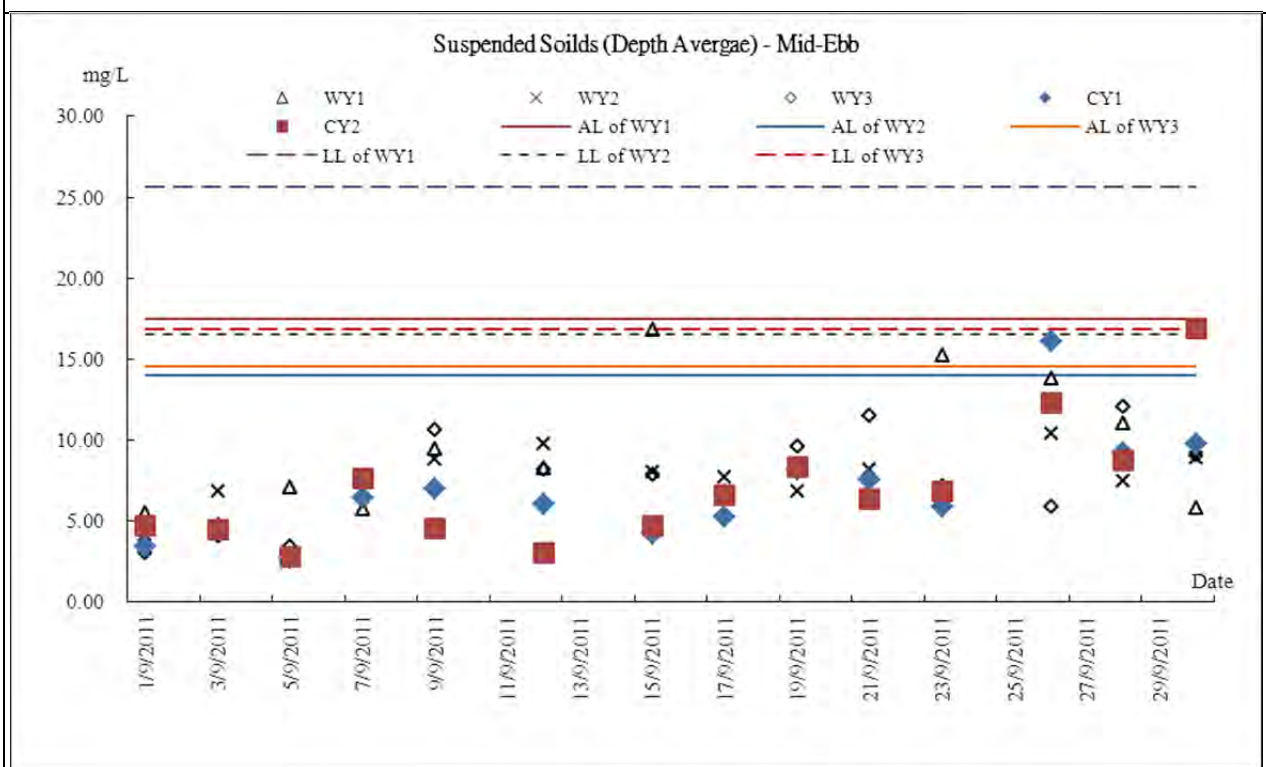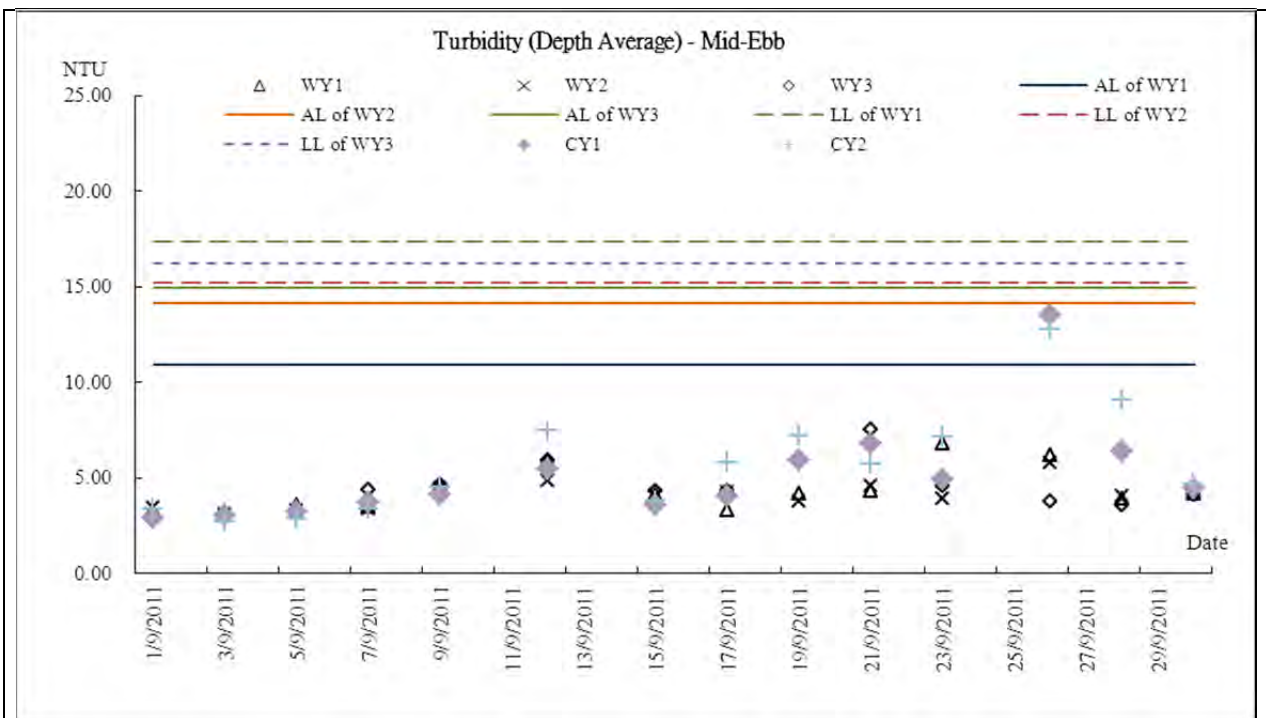

Marine Water Quality Monitoring – Mid Flood Tide

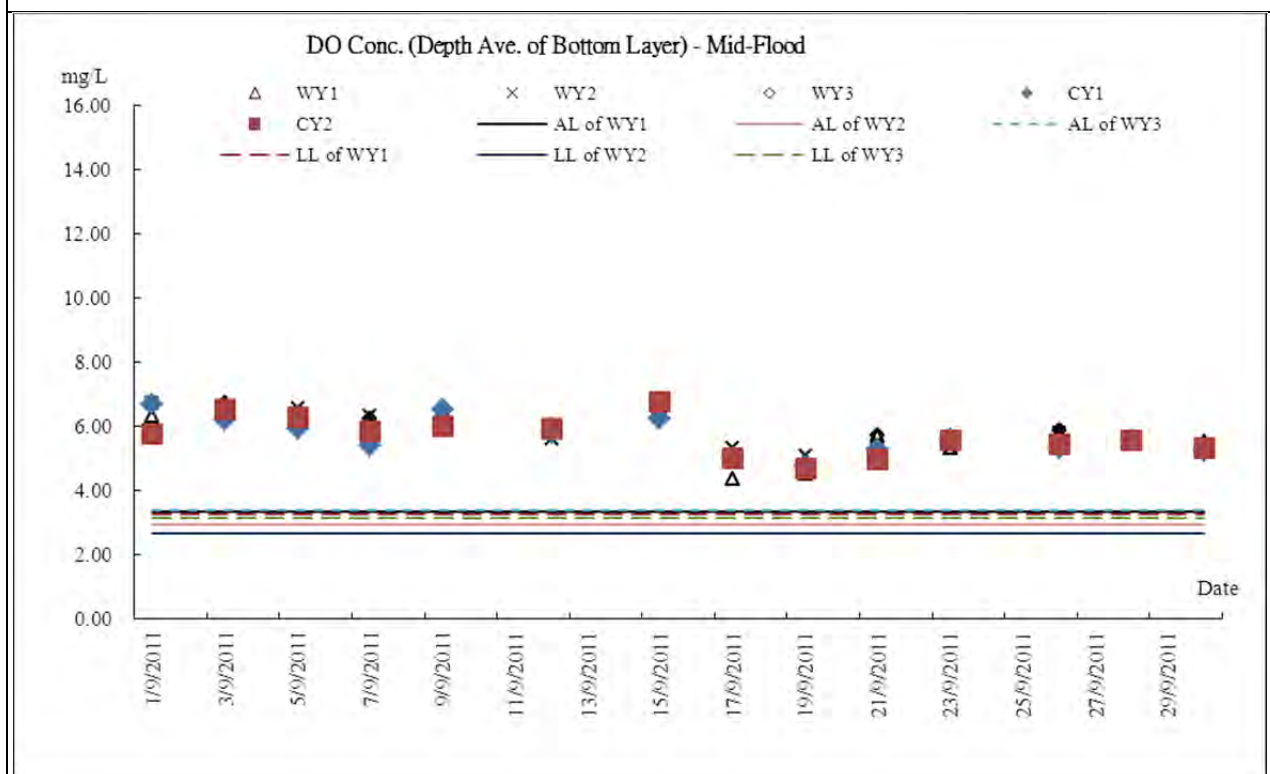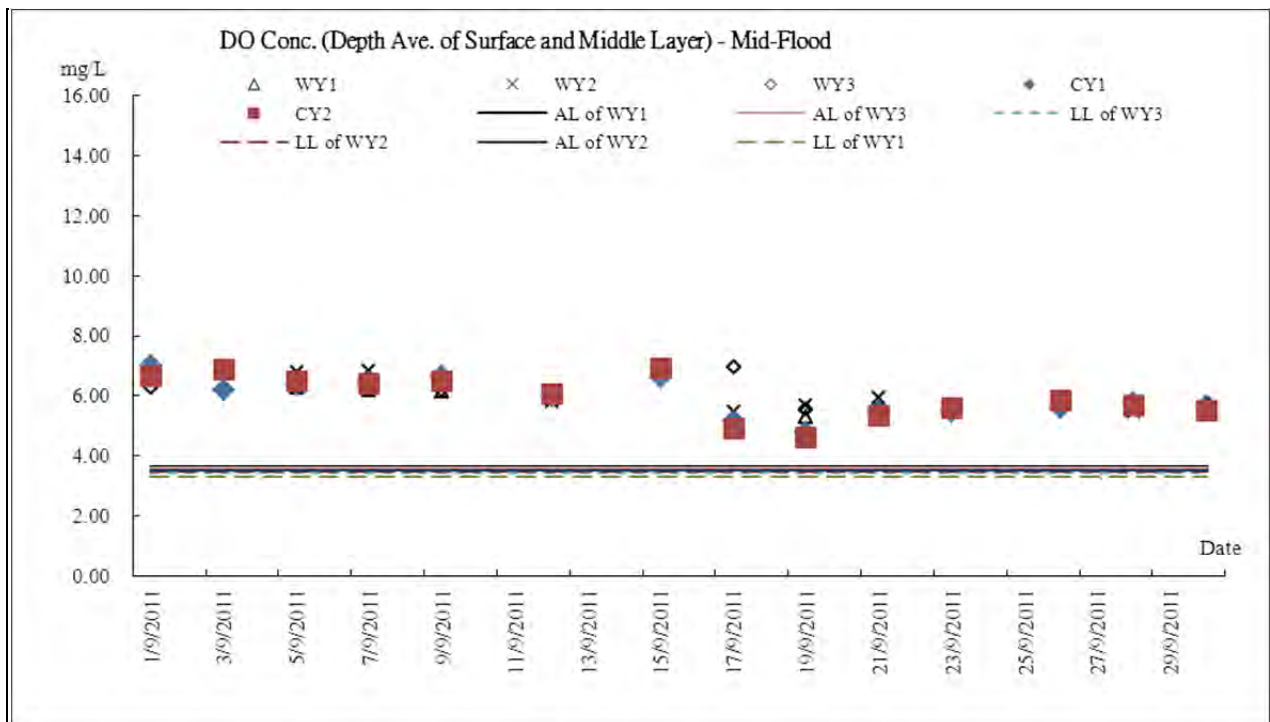

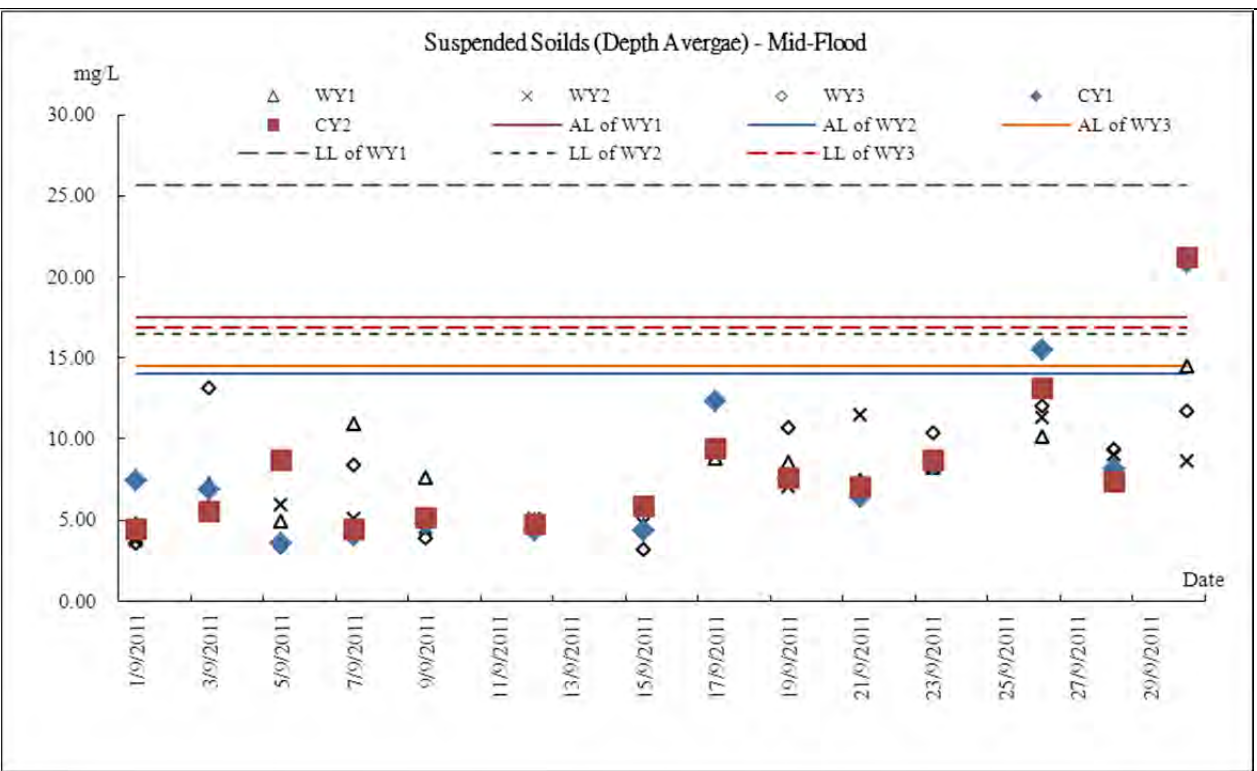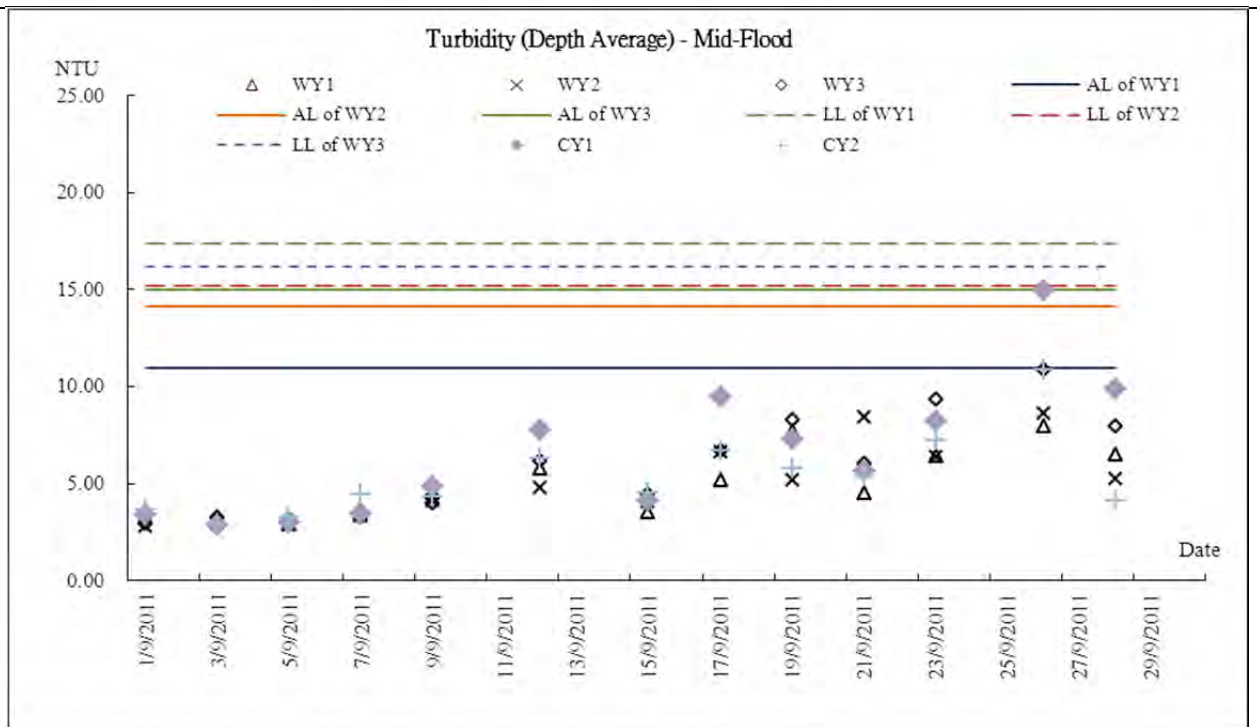

Appendix I

Meteorological Information

Meteorological Data Extracted from HKO during the Reporting Period

Date		Weather
1-Sep-11	Thu	Mainly cloudy with isolated showers.
2-Sep-11	Fri	Light to moderate easterly winds.
3-Sep-11	Sat	Light to moderate southeasterly winds.
4-Sep-11	Sun	Mainly fine apart from isolated showers.
5-Sep-11	Mon	Mainly fine.
6-Sep-11	Tue	fine and hot
7-Sep-11	Wed	Moderate southeasterly winds.
8-Sep-11	Thu	Sunny periods
9-Sep-11	Fri	Moderate to fresh easterly winds.
10-Sep-11	Sat	fine and hot
11-Sep-11	Sun	Fine and very hot.
12-Sep-11	Mon	Moderate to fresh northeasterly winds.
13-Sep-11	Tue	Mainly fine.
14-Sep-11	Wed	Moderate to fresh easterly winds.
15-Sep-11	Thu	Light to moderate southeasterly winds.
16-Sep-11	Fri	Mainly fine apart from isolated showers.
17-Sep-11	Sat	Moderate southeasterly winds.
18-Sep-11	Sun	fine and hot
19-Sep-11	Mon	A few showers
20-Sep-11	Tue	Light to moderate southwesterly winds.
21-Sep-11	Wed	Moderate to fresh northeasterly winds.
22-Sep-11	Thu	Mainly cloudy with a few light rain patches
23-Sep-11	Fri	Moderate southeasterly winds.
24-Sep-11	Sat	A few showers
25-Sep-11	Sun	Moderate to fresh easterly winds.
26-Sep-11	Mon	Mainly cloudy with occasional showers.
27-Sep-11	Tue	Moderate to fresh east to northeasterly winds
28-Sep-11	Wed	A few squally showers
29-Sep-11	Thu	NO. 8 SOUTHWEST GALE OR STORM SIGNAL
30-Sep-11	Fri	Mainly cloudy with occasional showers.

Appendix J

Monthly Summary Waste Flow Table

Monthly Summary Waste Flow Table for September 2011

Month	Actual Quantities of Inert C&D Materials Generated Monthly												Actual Quantities of C&D Wastes Generated Monthly										
	Total Quantity Generated (a) = (c)+(d)+(e)		Hard Rock and Large Broken Concrete (b)		Reused in the Contract (c)		Reused in other Projects (d)		Disposed as Public Fill (e)		Imported Fill (f)		Metals		Paper/ cardboard packaging		Plastics		Chemical Waste		Others, e.g. rubbish		
	(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in tonne)		
	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	
2010	4.522	0.030	0.068	0.104	0.488	0.000	0.000	0.000	0.000	4.033	0.030	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	18.460
Jan	0.985	3.045	0.003	0.013	0.120	0.419	0.000	2.626	0.865	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	2.240
Feb	0.377	0.000	0.000	0.043	0.000	0.000	0.000	0.000	0.377	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.350
Mar	0.758	1.175	0.002	0.106	0.006	0.000	0.000	1.175	0.752	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.360
Apr	1.135	1.339	0.017	0.025	0.112	0.180	0.000	1.159	1.023	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	2.830	5.160
May	0.614	1.362	0.030	0.036	0.014	0.400	0.000	0.962	0.600	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.150	0.860
Jun	0.505	1.014	0.000	0.022	0.000	0.060	0.000	0.954	0.505	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	9.610	1.510
Sub-total	8.8954	7.9653	0.1184	0.3497	0.7397	1.0590	0.0000	6.8760	8.1558	0.0303	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	0.0000	15.5900	28.9400
Jul	0.824	1.077	0.000	0.004	0.000	0.000	0.000	1.077	0.824	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	5.000	0.510
Aug	0.491	3.519	0.004	0.006	0.000	0.000	0.000	3.519	0.491	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	7.990	1.830
Sep	0.074	1.473	0.037	0.004	0.000	0.000	0.000	1.473	0.074	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	23.030	2.420
Oct																							
Nov																							
Dec																							
Total	10.2846	14.0343	0.1596	0.3640	0.740	1.059	0.000	12.945	9.5449	0.0303	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	51.61	33.70
	24.319		0.524		1.799		12.945		9.575		0.000		0.000		0.000		0.000		0.000		85.31		

Remark: Assume 1.0 m³ vehicle dump load = 1.6 tonnes C&D materials

YSW: Yung Shue Wan

SKW: Sok Kwu Wan

Appendix K

Weekly Site Inspection Checklist

Project: TCS/00512/09
Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by _____
ETL/ ET's Representative: Ray Cheung
RE's Representative: C.C. Cheung
Contractor's Representative: Edwin Leung
IEC's Representative: _____

Date: 6 September 2011

Time: 11:00

PART A: GENERAL INFORMATION

Weather: Sunny Fine Cloudy Rainy
 Temperature: 29.3 °C
 Humidity: High Moderate Low
 Wind: Strong Breeze Light Calm

Environmental Permit No.

EP- 282/2007

Area Inspected

1 Yung Shue Wan

PART B: SITE AUDIT

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance;	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
	Follow Up: Observations requiring follow-Up actions N/A: Not Applicable						

Section 1: Water Quality

		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Remark 1
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.22	Are the oil interceptors/grease traps maintained properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.23	Is used bentonite recycled where appropriate?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 2: Air Quality							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must remove form site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 3: Noise							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 4: Waste/Chemical Management							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Are the chemical waste containers properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.08	Is the chemical waste storage area properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 5: Landscape & Visual							
5.01	Are retained and transplanted trees in health condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Project: TCS/00512/09
Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by _____
ETL/ ET's Representative: Ray Cheung
RE's Representative: C.C. Cheung
Contractor's Representative: Edwin Leung
IEC's Representative: _____

Date: 14 September 2011

Time: 11:00

PART A: GENERAL INFORMATION

Environmental Permit No.

Weather: Sunny Fine Cloudy Rainy
 Temperature: °C
 Humidity: High Moderate Low
 Wind: Strong Breeze Light Calm

EP- 282/2007

Area Inspected

1 Yung Shue Wan

PART B: SITE AUDIT

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance;	Not Obs.	Yes	No	Follow Up	N/A	Photo/ Remarks
	Follow Up: Observations requiring follow-up actions N/A: Not Applicable						

Section 1: Water Quality

		Not Obs.	Yes	No	Follow Up	N/A	Photo/ Remarks
1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.22	Are the oil interceptors/grease traps maintained properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.23	Is used bentonite recycled where appropriate?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 2: Air Quality							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must remove form site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 3: Noise							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 4: Waste/Chemical Management							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Are the chemical waste containers properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.08	Is the chemical waste storage area properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 5: Landscape & Visual							
5.01	Are retained and transplanted trees in health condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/ Remarks
5.02	Are retained and transplanted trees properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 7: Others							
7.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
7.02	Are the warning sign or larvicidal oil record shown clearly at the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Remarks

Findings of Site Inspection (14 September 2011):

Follow up:

No environmental issue was observed during the site inspection.

IEC's representative RE's representative ET's representative EO's representative Contractor's representative

Ray

() () (Ray Cheung) () ()

Project: TCS/00512/09
Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by _____
ETL/ ET's Representative: F.N. Wong
RE's Representative: C.C. Cheung
Contractor's Representative: Edwin Leung
IEC's Representative: Selina Leung
Date: 20 September 2011 **Time:** 12:00

Checklist No. TCS512A200911
Environmental Permit No. EP- 282/2007

PART A: GENERAL INFORMATION

Weather: Sunny Fine Cloudy Rainy

Temperature: °C

Humidity: High Moderate Low

Wind: Strong Breeze Light Calm

Area Inspected
 1 Yung Shue Wan

PART B: SITE AUDIT

Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
---	-----------------	------------	-----------	------------------	------------	----------------------

Section 1: Water Quality

1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.22	Are the oil interceptors/grease traps maintained properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.23	Is used bentonite recycled where appropriate?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 2: Air Quality							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must remove form site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 3: Noise							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 4: Waste/Chemical Management							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Are the chemical waste containers properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.08	Is the chemical waste storage area properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 5: Landscape & Visual							
5.01	Are retained and transplanted trees in health condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
5.02	Are retained and transplanted trees properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 7: Others							
7.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
7.02	Are the warning sign or larvicidal oil record shown clearly at the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Remarks

Findings of Site Inspection (20 September 2011):

Follow up:

No environmental issue was observed during the site inspection.

IEC's representative RE's representative ET's representative EO's representative Contractor's representative



() () (F.N. Wong) () ()

Project: TCS/00512/09
Construction of Sewage Treatment Works at
Yung Shue Wan and Sok Kwu Wan

Inspected by _____
ETL/ ET's Representative: F.N. Wong
RE's Representative: C.C. Cheung
Contractor's Representative: Edwin Leung
IEC's Representative: _____

Date: 27 September 2011

Time: 11:00

PART A: GENERAL INFORMATION

Weather: Sunny Fine Cloudy Rainy
 Temperature: °C
 Humidity: High Moderate Low
 Wind: Strong Breeze Light Calm

Environmental Permit No.

EP- 282/2007

Area Inspected

1 Yung Shue Wan

PART B: SITE AUDIT

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance;	Not Obs.	Yes	No	Follow Up	N/A	Photo/ Remarks
	Follow Up: Observations requiring follow-Up actions N/A: Not Applicable						

Section 1: Water Quality

		Not Obs.	Yes	No	Follow Up	N/A	Photo/ Remarks
1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.22	Are the oil interceptors/grease traps maintained properly?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.23	Is used bentonite recycled where appropriate?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m ³ capacities for sedimentation.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 2: Air Quality							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must remove form site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 3: Noise							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 4: Waste/Chemical Management							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.06	Are the chemical waste containers properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.08	Is the chemical waste storage area properly labelled?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 5: Landscape & Visual							
5.01	Are retained and transplanted trees in health condition?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
5.02	Are retained and transplanted trees properly protected?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 7: Others							
7.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
7.02	Are the warning sign or larvicidal oil record shown clearly at the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Remarks

Findings of Site Inspection (27 September 2011):

Follow up:

No environmental issue was observed during the site inspection.

IEC's representative RE's representative ET's representative EO's representative Contractor's representative



() () (F.N. Wong) () ()

Appendix L

Implementation Schedule of Mitigation Measures

Implementation Schedule of Air Quality Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.3.18	2.10.2	Adopting the following good site practices and follow the dust control requirements of the Air Pollution Control (Construction Dust) Regulation: <ul style="list-style-type: none"> • Stockpiles of imported material kept on site should be contained within hoardings, dampened and / or covered during dry and windy weather; • Material stockpiled alongside trenches should be covered with tarpaulins whenever works are close to village houses; • Water sprays should be used during the delivery and handling of cement, sands, aggregates and the like. • Any vehicle used for moving sands, aggregates and construction waste should have properly fitting side and tail boards. Materials should not be loaded to a level higher than the side and tail boards, and should be covered by a clean tarpaulin. 	Work site / during construction	All contractors		√		TM- EIAO, APCO, Air Pollution Control (Construction Dust) Regulation
2.10.3	Section 2	1 hour and 24 hour dust monitoring and site audit	Designated air monitoring locations / throughout construction period	Contractor/ Environmental Team		√		EM&A Manual

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Noise Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location/Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.4.16	3.8.2	Implementation of following measures during the sewer construction: <ul style="list-style-type: none"> • Use of quiet PME or method; • Restriction on the number plant (1 item for each type of plant); and • Good Site Practices <ul style="list-style-type: none"> ➤ Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme. ➤ Mobile plant, if any, should be sited as far away from NSRs as possible. ➤ Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum. ➤ Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. ➤ Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. 	Work site /during the construction of Sewer.	Contractor		√		EIAO-TM, NCO
2.10.5 to 2.10.9	Section 35	Noise monitoring	Designated noise monitoring locations / throughout construction period	Contractor/ Environmental Team		√		EM&A Manual

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Water Quality Control Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
Construction Phase								
2.5.23	4.12.1	No-dig method using Horizontal Directional Drilling (HDD) would be used for the installation of main portion of outfall pipes	Marine works site / During construction of submarine outfall	Contractor		√		
4.5.38	4.12.3	<p>Dredging Works</p> <p>Implementation of following measures during the dredging works:</p> <ul style="list-style-type: none"> dredging should be undertaken using closed grab dredgers with a maximum total production rate of 55m³/hr; deployment of 2-layer silt curtains with the first layer enclosing the grab and the second layer at around 50m from the dredging area while dredging works are in progress; dredging operation should be undertaken during ebb tide only; all vessels should be sized such that adequate clearance (i.e. minimum clearance of 0.6m) is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; all pipe leakages should be repaired promptly and plant should not be operated with leaking pipes; excess material should be cleaned from the decks and exposed fittings of barges before the vessel is moved; adequate freeboard (i.e. minimum of 200mm) should be maintained on barges to ensure that decks are not washed by wave action; all barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; loading of barges should be controlled to prevent splashing of dredged material to the surrounding water, and barges should not be filled to a level which will cause the overflow of materials or polluted water during loading or transportation; and 	Marine works site and at the identified water sensitive receivers/ During construction	Contractor		√		

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
		<ul style="list-style-type: none"> the decks of all vessels should be kept tidy and free of oil or other substances that might be accidentally or otherwise washed overboard. 						
2.5.39	4.12.4	<p><u>Construction Run-off and Drainage</u></p> <p>Implementation of the following site practices outlined in ProPECC PN 1/94 for “Construction Site Drainage”</p> <ul style="list-style-type: none"> Provision of perimeter channels to intercept storm-runoff from outside the site. These should be constructed in advance of site formation works and earthworks. Works programmes should be designed to minimize works areas at any one time, thus minimizing exposed soil areas and reducing the potential for increased siltation and runoff. Sand / silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove the sand / silt particles from run-off. These facilities should be properly and regularly maintained. These facilities should be carefully planned to ensure that they would be installed at appropriate locations to capture all surface water generated on site. Careful programming of the works to minimise soil excavation works during rainy seasons. Exposed soil surface should be protected by paving or hydroseeding as soon as possible to reduce the potential of soil erosion. Trench excavation should be avoided in the wet season, and if necessary, these should be excavated and backfilled in short sections. Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric 	Construction works sites	Contractor		√		ProPECC PN 1/94
2.5.39	4.12.5	<p><u>General Construction Activities</u></p> <ul style="list-style-type: none"> Debris and rubbish generated on-site should be collected, handled and disposed of properly to avoid entering the nearby coastal waters and stormwater drains. 	Construction works sites	Contractor		√		

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
		<ul style="list-style-type: none"> All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Open drainage channels and culverts near the works areas should be covered to block the entrance of large debris and refuse. 						
2.5.39	4.12.6	<u>Wastewater Arising from Workforce</u> Portable toilets should be provided by the Contractors, where necessary, to handle sewage from the workforce. The Contractor should also be responsible for waste disposal and maintenance practices.	Construction works sites	Contractor		√		
2.10.10	Section 4	Water quality monitoring	Designated water monitoring locations/ throughout construction period	Contractor		√		EM&A Manual

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Sediment Contamination Mitigation Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
2.9.24	5.2.1	Carrying out Sediment Quality Investigation	Marine works site / prior to construction	DSD	√			WBTC No. 34/2002
2.9.23	5.2.1	Follow the requirement and procedures for dredged mud disposal specified under the WBTC No. 34/2002.	Marine works site / during dredging works	Contractor		√		WBTC No. 34/2002
2.9.23	5.2.2	Implement appropriate dredging methods which have been incorporated into the recommended water quality mitigation measures.	Marine works site, during dredging works	Contractor		√		
2.9.23	5.2.3	During the transportation and disposal of the dredged sediment, the following measures should be taken: <ul style="list-style-type: none"> • Bottom opening of barges should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved. • Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self monitoring devices as specified by the DEP. 	Marine works site and at the identified sensitive receivers	Contractor		√		

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Solid Waste Management Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.9.14	6.6.2	<u>Good site practices</u> <ul style="list-style-type: none"> Nomination of an approved person, such as a site manager, to be responsible for implementation of good site practices, arranging for collection and effective disposal to an appropriate facility, of all wastes generated at the site Training (proper waste management and chemical handling procedure) should be provided for site staffs Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers. Provision of sufficient waste disposal points and regular collection for disposal. Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility. Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. Maintain records of the quantities of wastes generated, recycled and disposed. 	Work sites/During construction	Contractor		√		Waste Disposal Ordinance (Cap.54)
2.9.15	6.2.3	The Contractor will be required to open a billing account under the Construction Waste Disposal Charging Scheme, and to pay for disposal of all construction waste. The construction waste will be sent to a designated reception facility, which in this case will be YSW RTS, where drivers must present a valid chit for disposal of each load.	Work sites/During construction	Contractor		√		Waste disposal (Amendment) Ordinance 2004
2.9.16	6.2.4	Recommendations to achieve waste reduction include: <ul style="list-style-type: none"> segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; to encourage collection of aluminium cans by individual collectors, separate labelled bins should be provided to 	Work sites/During construction	Contractor		√		WBTC No. 4/98, 5/98

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
		segregate this waste from other general refuse generated by the work force; <ul style="list-style-type: none"> any unused chemicals or those with remaining functional capacity should be recycled; use of reusable non-timber formwork to reduce the amount of C&D material; prior to disposal of C&D waste, it is recommended that wood, steel and other metals should be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill; proper storage and site practices to minimise the potential for damage or contamination of construction materials; and plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 						
2.9.18	6.2.5	<u>General Site Wastes</u> <ul style="list-style-type: none"> A collection area for construction site waste should be provided where waste can be stored prior to removal from site An enclosed and covered area for the collection of the waste is recommended to reduce 'wind blow' of light material 	Work sites/During construction	Contractor		√		Public Health and Municipal Services Ordinance (Cap. 132)
2.9.19	6.2.6 and 6.2.7	<u>Chemical Wastes</u> <ul style="list-style-type: none"> After use, chemical waste should be handled according to the Code of Practice on the Package, Labelling and Storage of Chemical Wastes Any unused chemicals or those with remaining functional capacity should be recycled Waste should be properly stored on site within suitably designed containers and should be collected by an approved licensed waste collectors for disposal at the Chemical Waste Treatment Facility or other licenced facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation under the Waste Disposal Ordance. 	Work sites/During construction	Contractor		√		Waste Disposal (Chemical Waste) (General) Regulation, Code of Practice on the Packaging Labelling and Storage of Chemical Wastes

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
		<ul style="list-style-type: none"> Any service shop and minor maintenance facilities should be located on hard standing within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should be undertaken within the designated areas equipped control these discharges 						
2.9.21 and 2.9.22	6.2.8 and 6.2.9	<p><u>Construction and Demolition Material</u></p> <ul style="list-style-type: none"> The C&D waste should be separated on-site into three categories: <ul style="list-style-type: none"> ➤ public fill, the inert portion of the C&D material (e.g. concrete and rubble), which should be re-used on-site or disposed of at a public filling area; ➤ C&D waste for re-use and / or recycling, the non-inert portion of the C&D material, (e.g. steel and other metals, woods, glass and plastic); ➤ C&D waste which cannot be re-used and / or recycled (e.g. wood, glass and plastic) Where possible, inert material should be re-used on-site Where practicable, steel and other metals should be separated for re-use and/or recycling prior to disposal of C&D material 	During all construction phases	Contractors		√		WBTC No. 4/98, 5/98, 21/2002, 25/99, 12/2000

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Ecological Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.10.11 and 2.10.12	7.2 and 7.3	Carry out monitoring of corals before, during and after marine works.	Work sites / during construction phase	Contractor		√		
2.6.45 to 2.6.48	7.6.1	Use horizontal directional drilling to avoid direct disturbance to corals	Marine works site / during dredging works	Contractor		√		
2.6.57 to 2.6.58	4.12.3	Deploying of 2-layer silt curtains with the first layer enclosing the grab and the second layer at around 50m from the dredging area while dredging works are in progress	All work sites / during construction phase	Contractor		√		
2.6.51	7.6.1	Fence off the slope stabilisation works area from surrounding shrubland and/ woodland, to prevent access to or disturbance of adjacent habitats. The works area should be as small as is possible, consistent with the requirements of the works.	STW/ During construction	Contractor		√		

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Fisheries Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
2.5.37	4.12.4	Use of closed grab dredging and silt curtains around the immediate dredging area and low dredging rates as recommended in Water Quality of the EIA report	Marine works site, during dredging works	Contractor		√		TM on EIA Process

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.
 ** D=Design, C=Construction, O=Operation
 N/A Not applicable

Implementation Schedule of Landscape and Visual Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.8.37	9.2.2	Careful and efficient transplanting of affected trees to temporary or final transplant location (the proposed tree to be transplanted is a semi-mature <i>Macaranga tanarius</i> and is located at the proposed Pumping Station P2 location).	All sites	Contractor		√		WBTC No. 14/2002
2.8.37	9.2.2	Short excavation and immediate backfilling sections upon completion of works to reduce active site area.	All sites	Contractor		√		
2.8.37	9.2.2	Screening of site construction works by use of hoarding that is appropriate to its site.	All sites	Contractor		√		WBTC No. 19/2001
2.8.37	9.2.2	Conservation of topsoil for reuse.	All sites	Contractor		√		
2.8.30	9.2.2	Night-time light source from marine fleets should be directed away from the residential units.	Outfall area.	Contractor		√		

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.
 ** D=Design, C=Construction, O=Operation
 N/A Not applicable

Appendix M

Impact Coral Monitoring Report

1. BACKGROUND

- 1.1 Further to the Sewerage Master Plan (SMP) study of the Outlying Islands in 1994, Drainage Services Department (DSD) was commissioned by Environmental Protection Department (EPD) to carry out a Preliminary Project Feasibility Study (PPFS) for the Outlying Islands Sewerage Stage I Phase II in 1996. The project is part of an Outlying Islands Sewerage Project, which involves construction of a sewage treatment works (STW) and submarine outfalls of approximately 500m in length and 325mm in diameter at Yung Shue Wan (YSW) on Lamma Island. Coral colonies were recorded at YSW site during the Environmental Impact Assessment (EIA) under the Preliminary Investigations Study (PIS).
- 1.2 As construction works of marine outfall was commenced on 9 May 2011 and coral monitoring is required in this reporting month. This coral monitoring report present the result coral monitoring exercise of corals at YSW and SW in September 2011 following the tagging for 20 corals on both sites for the Contract No. DC/2009/13 - Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan.

2. MONITORING EQUIPMENT

- 2.1 The monitoring equipment used for the coral monitoring are listed in **Table 2-1**.

Table 2-1 Monitoring Equipment for the Coral Monitoring

Equipment	Model
A4 size underwater slates	Handmade A4 size underwater slates
Coral Photos	Laminated Tagged Coral Photos
Quadrat	50 cm x 50 cm plastic quadrat (with 10 cm x 10 cm grid)
Underwater Camera	Canon G10 digital camera
Scuba Diving Equipment	Scubapro regulator, BCD and fins
Diving Boat	33 feet long diving boat with two 200hp outboard engines, registration #128328

3. MONITORING LOCATION

- 3.1 One control station at Sham Wan, Lamma Island and one impact stations at boulder seawall at Yung Shue Wan, Lamma Island were recommended in the *Method Statement Section 3.3*. These sites represent the coral site where uncommon coral species were recorded from the coral surveys carried out as part of the Review Report on the EIA Study. The coordinates of the monitoring location is listed in **Table 3-1**.

Table 3-1 Locations of Coral Monitoring Station

Dive Site	Coordinates	
	Easting	Northing
Yung Shue Wan, Lamma Island	829180.06E	809555.76N
Sham Wan, Lamma Island	832160.86E	805738.31N

4. METHODOLOGY

- 4.1 20 tagged hard coral colonies were monitored at the impact (Yung Shue Wan) and control station (Sham Wan). Laminated photos of the tagged corals were used underwater to relocate and identify the tagged corals.
- 4.2 Three parameters were recorded for each tagged coral and these are:
- Percentage sediment cover
 - Increase % sediment cover caused by marine work will affect the health of

coral as it will block the sunlight that reaches the corals, this may result in bleaching or death of the coral colonies.

- Percentage bleached tissue – two bleaching categories will be recorded;
 - Unhealthy corals will show bleached tissue especially when sediment and turbidity increased, prolonged bleaching may result in total or partial death of the coral colonies.
 - Bleached or pale – a loss of zooxanthellae or photosynthetic pigments
 - Bleached – a total loss zooxanthellae and coral tissue still present
 - Percentage dead – total or partial mortality.
 - Increased in total or partial mortality rate may be caused by the marine work.
- 4.3 Each parameter was assessed as a percentage of total colony area. To aid percentage cover estimates a 50 x 50 cm² quadrat with a 10x10 cm² lined grid was used.
- 4.4 During each survey, diversity, abundance and health status of the corals in the general area will be recorded.
- 4.5 Photos of each tagged corals were also taken during the monitoring survey.

5. RESULTS

- 5.1 Coral monitoring was carried out on 9th, 15th, 22nd and 28th September 2011. The weather conditions were summarised in **Table 5-1**.

Table 5-1 Weather Conditions on 9th, 15th, 22nd and 28th September 2011

Date	9 th September		15 th September		22 nd September		28 th September	
	YSW	SW	YSW	SW	YSW	SW	YSW	SW
Survey Time	9:00	8:00	9:00	8:00	9:00	8:00	9:00	8:00
Tidal Height	2.1m		1.7m		1.4m		2.1m	
Air Temperature	32° C		32° C		29° C		25° C	
Water Temperature	22° C		21° C		21° C		21° C	
Water Depth	2m	2.5m	2m	2.5m	2m	2.5m	2m	2.5m
Wind Speed	East to Southeast 3-4		East to Southeast 3-4		Northeast 5		Northeast 5	
Weather	Sunny		Sunny		Sunny		Sunny	
Water Visibility	0.5m	1m	<0.5m	1.5m	<0.3m	1m	<0.2m	0.5m

Yung Shue Wan

- 5.2 This site is mainly composed of artificial sloping boulders down to 2.5 meters depth along coral area. Areas deeper than 3 meters are mainly muddy and sandy bottoms. The coral coverage was about 5% in which most of them were located on the artificial sloping boulders. 20 hard coral colonies were monitored on 5th, 10th and 25th September 2011 and their species name, size and health condition were shown in **Table 5-2** to **Table 5-5**.
- 5.3 No sediment was recorded during the survey. No bleaching or mortality was recorded during the monitoring survey on the monitoring dates. Photos of each tagged corals were shown in **Appendix II**.

5.4 In general the diversity and abundance of corals in this area is relatively low and common respectively when compared with other coral area in Hong Kong such as Hoi Ha Wan and Sharp Island.

Table 5-2 Species Name, Size and Health Condition for Tagged Corals in YSW on 9th September 2011

Site: Yung Shue Wan				Sediment Cover (%)	Bleaching (%)		Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)		Blanched/Pale	Bleached		
1	<i>Favites chinensis</i>	Boulder	32	0	0	0	0	N/A
2	<i>Favia speciosa</i>	Boulder	30	0	0	0	0	N/A
3	<i>Favites pentagona</i>	Boulder	38	0	0	0	0	N/A
4	<i>Favia fava</i>	Boulder	17	0	0	0	0	N/A
5	<i>Porites lutea</i>	Boulder	43	0	0	0	0	N/A
6	<i>Porites lobata</i>	Boulder	18	0	0	0	0	N/A
7	<i>Cyphastrea serailia</i>	Boulder	26	0	0	0	0	N/A
8	<i>Favites chinensis</i>	Boulder	22	0	0	0	0	N/A
9	<i>Favites pentagona</i>	Boulder	106	0	0	0	0	N/A
10	<i>Coscinaraea n. sp.</i>	Boulder	16	0	0	0	0	N/A
11	<i>Goniopora stutchburyi</i>	Boulder	45	0	0	0	0	N/A
12	<i>Favites pentagona</i>	Boulder	20	0	0	0	0	N/A
13	<i>Goniopora stutchburyi</i>	Boulder	28	0	0	0	0	N/A
14	<i>Porites lobata</i>	Boulder	42	0	0	0	0	N/A
15	<i>Goniastrea aspera</i>	Boulder	19	1	0	0	0	N/A
16	<i>Cyphastrea serailia</i>	Boulder	16	0	0	0	0	N/A
17	<i>Plesiastrea versipora</i>	Boulder	27	0	0	0	0	N/A
18	<i>Goniopora stutchburyi</i>	Boulder	23	0	0	0	0	N/A
19	<i>Cyphastrea serailia</i>	Boulder	21	0	0	0	0	N/A
20	<i>Porites lutea</i>	Boulder	52	0	0	0	0	N/A

Table 5-3 Species Name, Size and Health Condition for Tagged Corals in YSW on 15th September 2011

Site: Yung Shue Wan				Sediment Cover (%)	Bleaching (%)		Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)		Blanched/Pale	Bleached		
1	<i>Favites chinensis</i>	Boulder	32	0	0	0	0	N/A
2	<i>Favia speciosa</i>	Boulder	30	0	0	0	0	N/A
3	<i>Favites pentagona</i>	Boulder	38	0	0	0	0	N/A
4	<i>Favia fava</i>	Boulder	17	0	0	0	0	N/A
5	<i>Porites lutea</i>	Boulder	43	0	0	0	0	N/A
6	<i>Porites lobata</i>	Boulder	18	0	0	0	0	N/A

Site: Yung Shue Wan				Bleaching (%)			Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)	Sediment Cover (%)	Blanched/Pale	Bleached		
7	<i>Cyphastrea serailia</i>	Boulder	26	0	0	0	0	N/A
8	<i>Favites chinensis</i>	Boulder	22	0	0	0	0	N/A
9	<i>Favites pentagona</i>	Boulder	106	0	0	0	0	N/A
10	<i>Coscinaraea n sp.</i>	Boulder	16	0	0	0	0	N/A
11	<i>Goniopora stutchburyi</i>	Boulder	45	0	0	0	0	N/A
12	<i>Favites pentagona</i>	Boulder	20	0	0	0	0	N/A
13	<i>Goniopora stutchburyi</i>	Boulder	28	0	0	0	0	N/A
14	<i>Porites lobata</i>	Boulder	42	0	0	0	0	N/A
15	<i>Goniastrea aspera</i>	Boulder	19	0	0	0	0	N/A
16	<i>Cyphastrea serailia</i>	Boulder	16	0	0	0	0	N/A
17	<i>Plesiastrea versipora</i>	Boulder	27	0	0	0	0	N/A
18	<i>Goniopora stutchburyi</i>	Boulder	23	0	0	0	0	N/A
19	<i>Cyphastrea serailia</i>	Boulder	21	0	0	0	0	N/A
20	<i>Porites lutea</i>	Boulder	52	0	0	0	0	N/A

Table 5-4 Species Name, Size and Heath Condition for Tagged Corals in YSW on 22nd September 2011

Site: Yung Shue Wan				Bleaching (%)			Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)	Sediment Cover (%)	Blanched/Pale	Bleached		
1	<i>Favites chinensis</i>	Boulder	32	0	0	0	0	N/A
2	<i>Favia speciosa</i>	Boulder	30	0	0	0	0	N/A
3	<i>Favites pentagona</i>	Boulder	38	0	0	0	0	N/A
4	<i>Favia fava</i>	Boulder	17	0	0	0	0	N/A
5	<i>Porites lutea</i>	Boulder	43	0	0	0	0	N/A
6	<i>Porites lobata</i>	Boulder	18	0	0	0	0	N/A
7	<i>Cyphastrea serailia</i>	Boulder	26	0	0	0	0	N/A
8	<i>Favites chinensis</i>	Boulder	22	0	0	0	0	N/A
9	<i>Favites pentagona</i>	Boulder	106	0	0	0	0	N/A
10	<i>Coscinaraea n sp.</i>	Boulder	16	0	0	0	0	N/A
11	<i>Goniopora stutchburyi</i>	Boulder	45	0	0	0	0	N/A
12	<i>Favites pentagona</i>	Boulder	20	0	0	0	0	N/A
13	<i>Goniopora stutchburyi</i>	Boulder	28	0	0	0	0	N/A
14	<i>Porites lobata</i>	Boulder	42	0	0	0	0	N/A
15	<i>Goniastrea aspera</i>	Boulder	19	0	0	0	0	N/A
16	<i>Cyphastrea serailia</i>	Boulder	16	0	0	0	0	N/A
17	<i>Plesiastrea versipora</i>	Boulder	27	0	0	0	0	N/A

Site: Yung Shue Wan				Bleaching (%)			Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)	Sediment Cover (%)	Blanched/Pale	Bleached		
18	<i>Goniopora stutchburyi</i>	Boulder	23	0	0	0	0	N/A
19	<i>Cyphastrea serailia</i>	Boulder	21	0	0	0	0	N/A
20	<i>Porites lutea</i>	Boulder	52	0	0	0	0	N/A

Table 5-5 Species Name, Size and Health Condition for Tagged Corals in YSW on 28th September 2011

Site: Yung Shue Wan				Bleaching (%)			Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)	Sediment Cover (%)	Blanched/Pale	Bleached		
1	<i>Favites chinensis</i>	Boulder	32	0	0	0	0	N/A
2	<i>Favia speciosa</i>	Boulder	30	0	0	0	0	N/A
3	<i>Favites pentagona</i>	Boulder	38	0	0	0	0	N/A
4	<i>Favia fava</i>	Boulder	17	0	0	0	0	N/A
5	<i>Porites lutea</i>	Boulder	43	0	0	0	0	N/A
6	<i>Porites lobata</i>	Boulder	18	0	0	0	0	N/A
7	<i>Cyphastrea serailia</i>	Boulder	26	0	0	0	0	N/A
8	<i>Favites chinensis</i>	Boulder	22	0	0	0	0	N/A
9	<i>Favites pentagona</i>	Boulder	106	0	0	0	0	N/A
10	<i>Coscinaraea n sp.</i>	Boulder	16	0	0	0	0	N/A
11	<i>Goniopora stutchburyi</i>	Boulder	45	0	0	0	0	N/A
12	<i>Favites pentagona</i>	Boulder	20	0	0	0	0	N/A
13	<i>Goniopora stutchburyi</i>	Boulder	28	0	0	0	0	N/A
14	<i>Porites lobata</i>	Boulder	42	0	0	0	0	N/A
15	<i>Goniastrea aspera</i>	Boulder	19	0	0	0	0	N/A
16	<i>Cyphastrea serailia</i>	Boulder	16	0	0	0	0	N/A
17	<i>Plesiastrea versipora</i>	Boulder	27	0	0	0	0	N/A
18	<i>Goniopora stutchburyi</i>	Boulder	23	0	0	0	0	N/A
19	<i>Cyphastrea serailia</i>	Boulder	21	0	0	0	0	N/A
20	<i>Porites lutea</i>	Boulder	52	0	0	0	0	N/A

Sham Wan

- 5.5 This site is mainly composed of bedrocks and big boulders down to 3.5 meters depth along the surveyed route. Areas deeper than 4 meters are mainly sandy bottoms. The coral coverage was about 10% in which most of corals were located on boulders or rock surfaces. 20 hard coral colonies were monitored on 9th, 15th, 22nd and 28th September 2011 and their species name, size and health condition were shown in **Table 5-6 to Table 5-9**.
- 5.6 No sediment was recorded during the survey. No bleaching or mortality was recorded during the monitoring survey on the monitoring dates. Photos of each tagged corals

were shown in **Appendix II**.

- 5.7 In general the diversity and abundance of corals in this area is relatively low and common respectively when compared with other coral area in Hong Kong such as Hoi Ha Wan and Sharp Island.

Table 5-6 Species Name, Size and Health Condition for Tagged Corals in SW on 9th September 2011

Site: Sham Wan				Bleaching (%)		Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)	Sediment Cover (%)	Blanched/Pale		
1	<i>Favia fавus</i>	Boulder	14	0	0	0	N/A
2	<i>Favia rotumana</i>	Boulder	21	0	0	0	N/A
3	<i>Favia rotumana</i>	Boulder	27	0	0	0	N/A
4	<i>Favia fавus</i>	Rock	14	0	0	0	N/A
5	<i>Goniopora stutchburyi</i>	Bedrock	32	0	0	0	N/A
6	<i>Porites lobata</i>	Bedrock	43	0	0	0	N/A
7	<i>Porites lobata</i>	Boulder	23	0	0	0	N/A
8	<i>Goniopora stutchburyi</i>	Bedrock	29	0	0	0	N/A
9	<i>Favites pentagona</i>	Bedrock	31	0	0	0	N/A
10	<i>Porites lobata</i>	Bedrock	34	0	0	0	N/A
11	<i>Porites lobata</i>	Boulder	33	0	0	0	N/A
12	<i>Coscinaraea n sp.</i>	Rock	15	0	0	0	N/A
13	<i>Cyphastrea serailia</i>	Bedrock	13	0	0	0	N/A
14	<i>Cyphastrea serailia</i>	Bedrock	12	0	0	0	N/A
15	<i>Favia fавus</i>	Boulder	14	0	0	0	N/A
16	<i>Favia rutomana</i>	Boulder	30	0	0	0	N/A
17	<i>Favia fавus</i>	Bedrock	26	0	0	0	N/A
18	<i>Favia rotumana</i>	Bedrock	28	0	0	0	N/A
19	<i>Cyphastrea serailia</i>	Bedrock	39	0	0	0	N/A
20	<i>Cyphastrea serailia</i>	Bedrock	27	0	0	0	N/A

Table 5-7 Species Name, Size and Health Condition for Tagged Corals in SW on 15th September 2011

Site: Sham Wan				Bleaching (%)		Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)	Sediment Cover (%)	Blanched/Pale		
1	<i>Favia fавus</i>	Boulder	14	0	0	0	N/A
2	<i>Favia rotumana</i>	Boulder	21	0	0	0	N/A
3	<i>Favia rotumana</i>	Boulder	27	0	0	0	N/A
4	<i>Favia fавus</i>	Rock	20	0	0	0	N/A
5	<i>Goniopora stutchburyi</i>	Bedrock	32	0	0	0	N/A

Site: Sham Wan				Bleaching (%)			Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)	Sediment Cover (%)	Blanched/Pale	Bleached		
6	<i>Porites lobata</i>	Bedrock	43	0	0	0	0	N/A
7	<i>Porites lobata</i>	Boulder	23	0	0	0	0	N/A
8	<i>Goniopora stutchburyi</i>	Bedrock	29	0	0	0	0	N/A
9	<i>Favites pentagona</i>	Bedrock	31	0	0	0	0	N/A
10	<i>Porites lobata</i>	Bedrock	34	0	0	0	0	N/A
11	<i>Porites lobata</i>	Boulder	33	0	0	0	0	N/A
12	<i>Coscinaraea n sp.</i>	Rock	15	0	0	0	0	N/A
13	<i>Cyphastrea serailia</i>	Bedrock	13	0	0	0	0	N/A
14	<i>Cyphastrea serailia</i>	Bedrock	12	0	0	0	0	N/A
15	<i>Favia fавus</i>	Boulder	14	0	0	0	0	N/A
16	<i>Favia rotumana</i>	Boulder	30	0	0	0	0	N/A
17	<i>Favia fавus</i>	Bedrock	26	0	0	0	0	N/A
18	<i>Favia rotumana</i>	Bedrock	28	0	0	0	0	N/A
19	<i>Cyphastrea serailia</i>	Bedrock	39	0	0	0	0	N/A
20	<i>Cyphastrea serailia</i>	Bedrock	27	0	0	0	0	N/A

Table 5-8 Species Name, Size and Health Condition for Tagged Corals in SW on 22nd September 2011

Site: Sham Wan				Bleaching (%)			Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)	Sediment Cover (%)	Blanched/Pale	Bleached		
1	<i>Favia fавus</i>	Boulder	14	0	0	0	0	N/A
2	<i>Favia rotumana</i>	Boulder	21	0	0	0	0	N/A
3	<i>Favia rotumana</i>	Boulder	27	0	0	0	0	N/A
4	<i>Favia fавus</i>	Rock	14	0	0	0	0	N/A
5	<i>Goniopora stutchburyi</i>	Bedrock	32	0	0	0	0	N/A
6	<i>Porites lobata</i>	Bedrock	43	0	0	0	0	N/A
7	<i>Porites lobata</i>	Boulder	23	0	0	0	0	N/A
8	<i>Goniopora stutchburyi</i>	Bedrock	29	0	0	0	0	N/A
9	<i>Favites pentagona</i>	Bedrock	31	0	0	0	0	N/A
10	<i>Porites lobata</i>	Bedrock	34	0	0	0	0	N/A
11	<i>Porites lobata</i>	Boulder	33	0	0	0	0	N/A
12	<i>Coscinaraea n sp.</i>	Rock	15	0	0	0	0	N/A
13	<i>Cyphastrea serailia</i>	Bedrock	13	0	0	0	0	N/A
14	<i>Cyphastrea serailia</i>	Bedrock	12	0	0	0	0	N/A
15	<i>Favia fавus</i>	Boulder	14	0	0	0	0	N/A
16	<i>Favia rotumana</i>	Boulder	30	0	0	0	0	N/A

Site: Sham Wan				Sediment Cover (%)	Bleaching (%)		Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)		Blanched/Pale	Bleached		
17	<i>Favia fавus</i>	Bedrock	26	0	0	0	0	N/A
18	<i>Favia rotumana</i>	Bedrock	28	0	0	0	0	N/A
19	<i>Cyphastrea serailia</i>	Bedrock	39	0	0	0	0	N/A
20	<i>Cyphastrea serailia</i>	Bedrock	27	0	0	0	0	N/A

Table 5-9 Species Name, Size and Heath Condition for Tagged Corals in SW on 28th September 2011

Site: Sham Wan				Sediment Cover (%)	Bleaching (%)		Total/Partial Mortality (%)	Remarks
Coral No.	Species Name	Specific Location	Size (cm) (Max. Length)		Blanched/Pale	Bleached		
1	<i>Favia fавus</i>	Boulder	14	0	0	0	0	N/A
2	<i>Favia rotumana</i>	Boulder	21	0	0	0	0	N/A
3	<i>Favia rotumana</i>	Boulder	27	0	0	0	0	N/A
4	<i>Favia fавus</i>	Rock	14	0	0	0	0	N/A
5	<i>Goniopora stutchburyi</i>	Bedrock	32	0	0	0	0	N/A
6	<i>Porites lobata</i>	Bedrock	43	0	0	0	0	N/A
7	<i>Porites lobata</i>	Boulder	23	0	0	0	0	N/A
8	<i>Goniopora stutchburyi</i>	Bedrock	29	0	0	0	0	N/A
9	<i>Favites pentagona</i>	Bedrock	31	0	0	0	0	N/A
10	<i>Porites lobata</i>	Bedrock	34	0	0	0	0	N/A
11	<i>Porites lobata</i>	Boulder	33	0	0	0	0	N/A
12	<i>Coscinaraea n sp.</i>	Rock	15	0	0	0	0	N/A
13	<i>Cyphastrea serailia</i>	Bedrock	13	0	0	0	0	N/A
14	<i>Cyphastrea serailia</i>	Bedrock	12	0	0	0	0	N/A
15	<i>Favia fавus</i>	Boulder	14	0	0	0	0	N/A
16	<i>Favia rutomana</i>	Boulder	30	0	0	0	0	N/A
17	<i>Favia fавus</i>	Bedrock	26	0	0	0	0	N/A
18	<i>Favia rotumana</i>	Bedrock	28	0	0	0	0	N/A
19	<i>Cyphastrea serailia</i>	Bedrock	39	0	0	0	0	N/A
20	<i>Cyphastrea serailia</i>	Bedrock	27	0	0	0	0	N/A







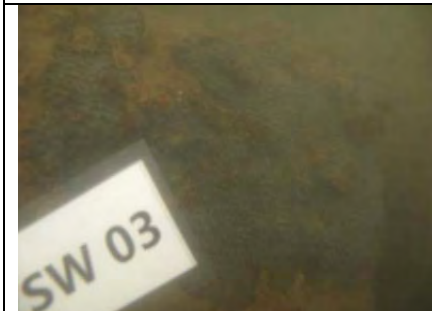



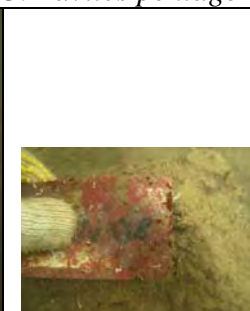

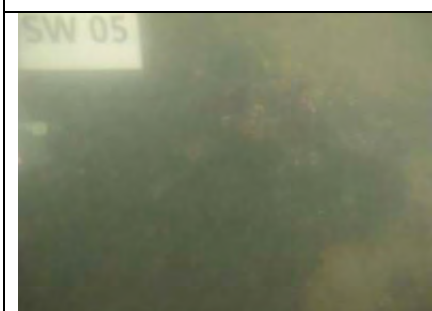

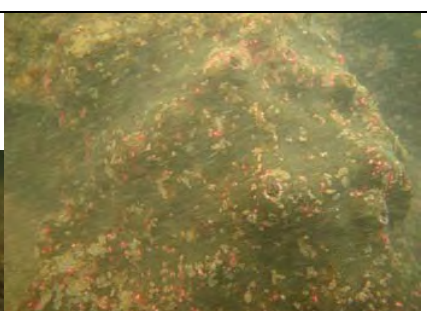
6. COMMENTS AND CONCLUSION










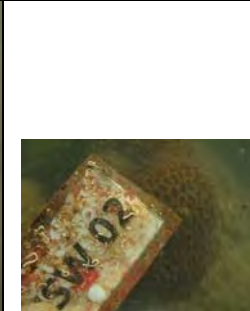




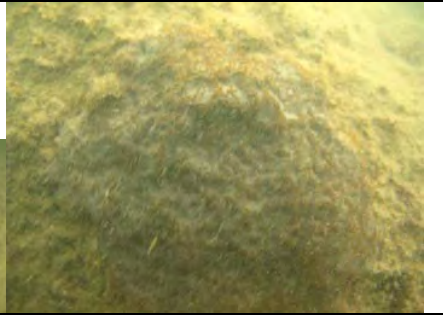
- 6.1 Coral monitoring were performed on 9th, 15th, 22nd and 28th September 2011 at Yung Shue Wan and Sham Wan and 20 hard coral colonies were monitored at each sites.
- 6.2 No sediment was recorded during the survey in both sites. No beaching was recorded on both sites during the monitoring period. No mortality was recorded in Sham Wan, The coral coverage in both impact site (YSW) and control site (SW) are relatively

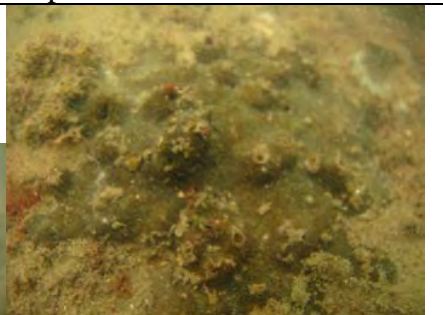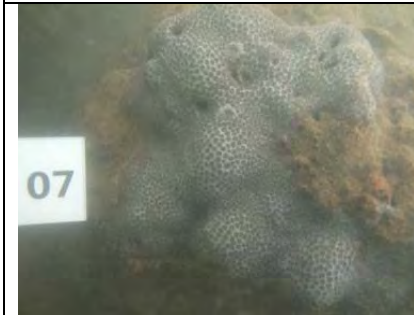

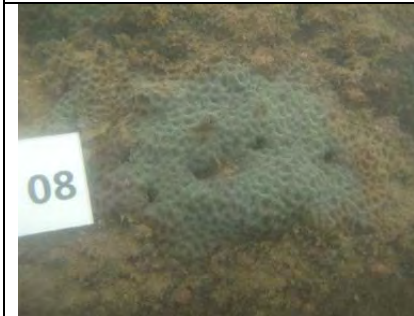












low when compared with other coral communities in Hong Kong (such as Sharp Island and Hoi Ha Wan). Most of the coral colonies recorded in both site are common species in Hong Kong water.






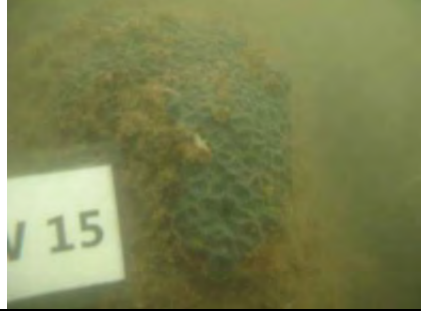


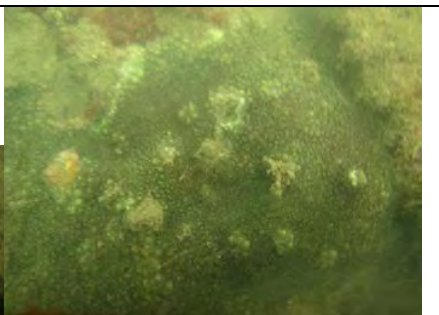
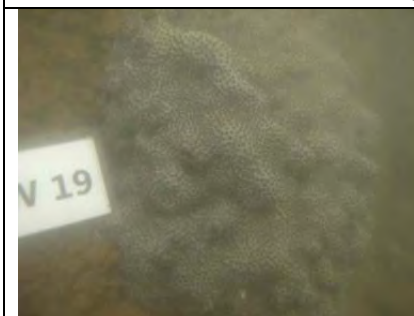


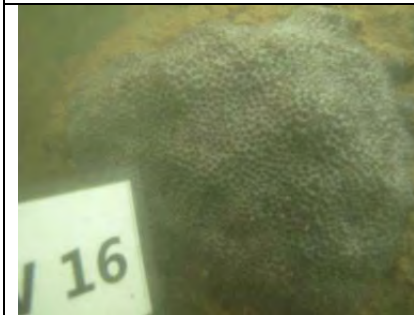


- 6.3 Partially mortality on the soft/black corals was not recorded at the monitoring site. No bleaching or deterioration in the general condition of the coral fauna was observed. No adverse deterioration of the coral community was observed in the ecological monitoring results when compared with the baseline ecological monitoring results.







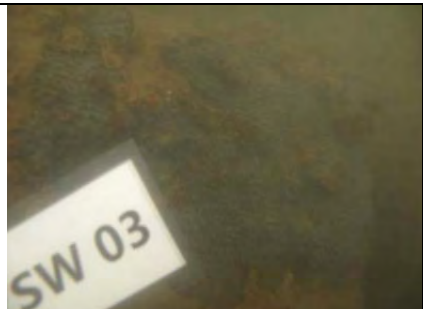

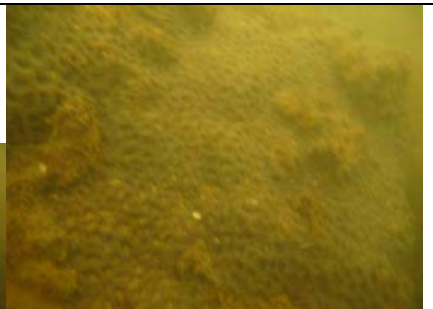






APPENDIX A Tagged Corals at Yung Shue Wan



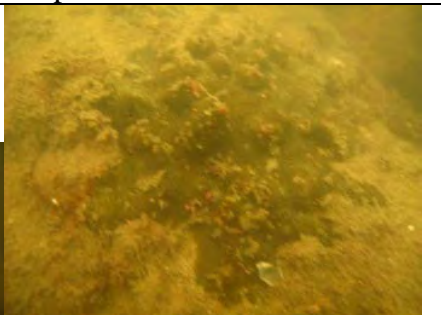
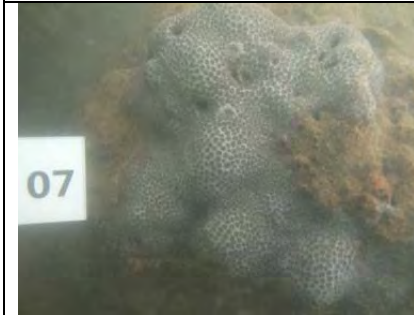

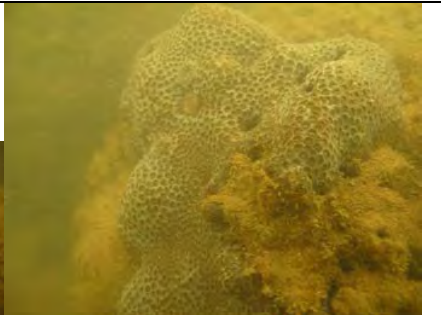

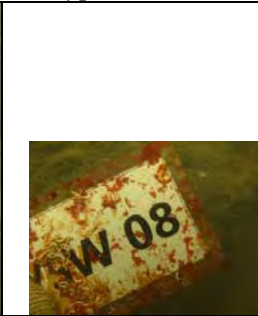




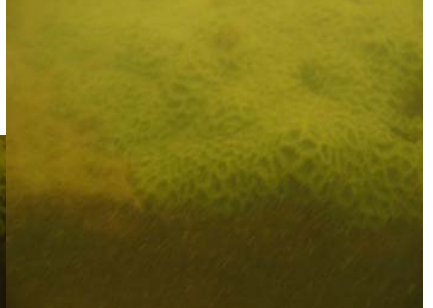


Baseline	9 th September 2011	
		
<i>Favites chinensis</i>		
		
02. <i>Favia speciosa</i>		
		
03. <i>Favites pentagona</i>		
		
04. <i>Favia fava</i>		
		
05. <i>Porites lutea</i>		

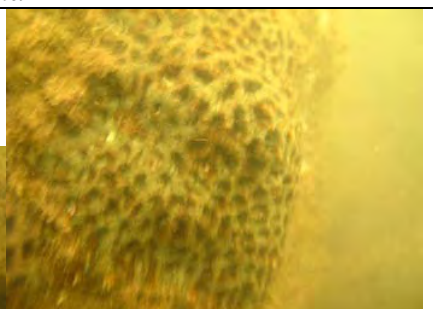








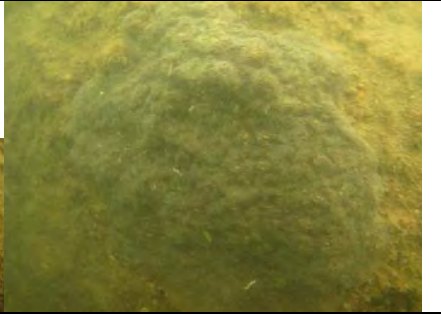





Baseline	9 th September 2011	
 <p>SW 06</p>	 <p>W 06</p>	
<i>06. Porites lobata</i>		
 <p>07</p>	 <p>SW 07</p>	
<i>07. Cyphastrea serailia</i>		
 <p>08</p>	 <p>08</p>	
<i>08. Favites chinensis</i>		
 <p>SW 09</p>	 <p>SW 09</p>	
<i>09. Favites pentagona</i>		
 <p>SW 10</p>	 <p>W 10</p>	
<i>10. Coscinaraea sp.</i>		




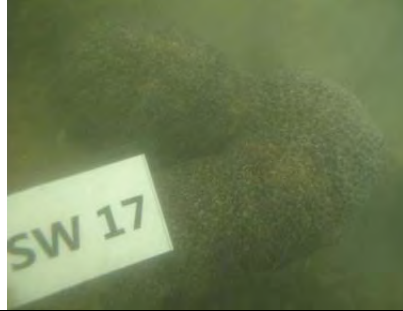











Baseline	9 th September 2011	
		
<i>11. Goniopora stutchburyi</i>		
		
<i>12. Favites pentagona</i>		
		
<i>13. Goniopora stutchburyi</i>		
		
<i>14. Porites lobata</i>		
		
<i>15. Goniastrea aspera</i>		



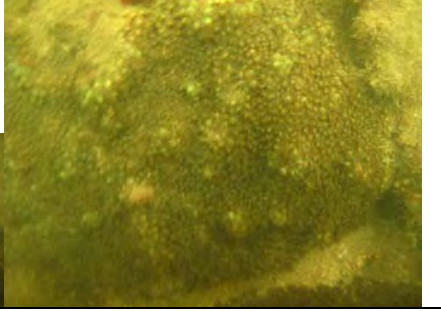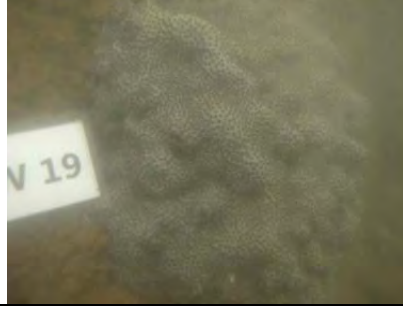


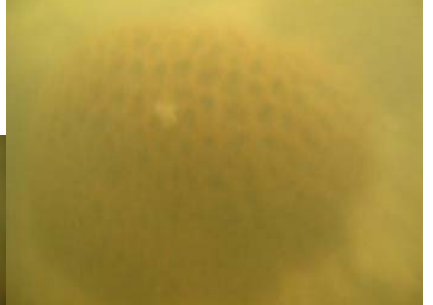
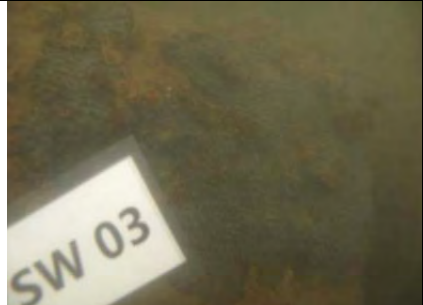








Baseline	9 th September 2011	
		
<i>16. Cyphastrea serailia</i>		
		
<i>17. Plesiastrea versipora</i>		
		
<i>18. Goniopora stutchburyi</i>		
		
<i>19. Cyphastrea serailia</i>		
		
<i>20. Porites lutea</i>		




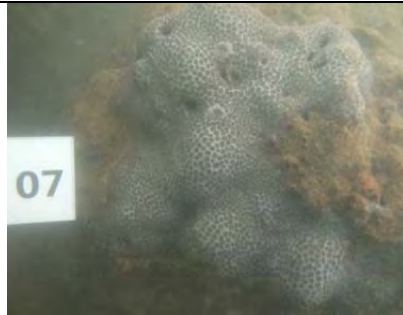


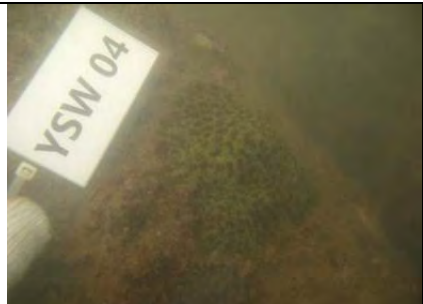




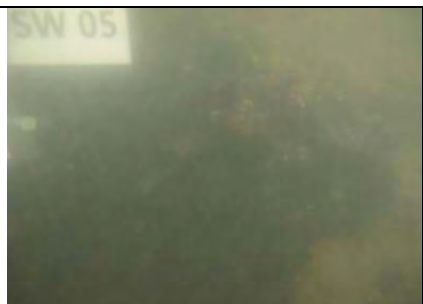



Baseline	15 th September 2011	
		
<i>Favites chinensis</i>		
		
02. <i>Favia speciosa</i>		
		
03. <i>Favites pentagona</i>		
		
04. <i>Favia fava</i>		
		
05. <i>Porites lutea</i>		








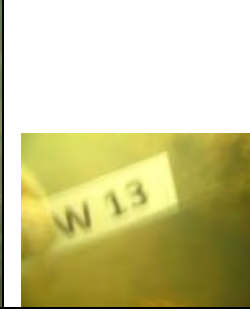







Baseline	15 th September 2011	
		
<i>06. Porites lobata</i>		
		
<i>07. Cyphastrea serailia</i>		
		
<i>08. Favites chinensis</i>		
		
<i>09. Favites pentagona</i>		
		
<i>10. Coscinaraea sp.</i>		




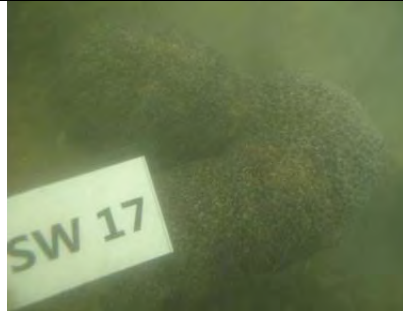


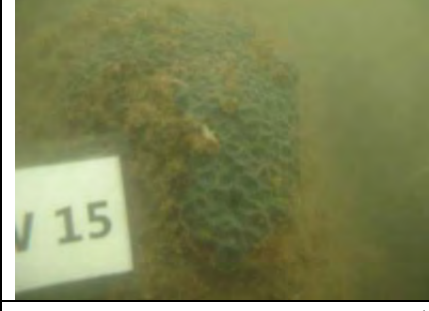


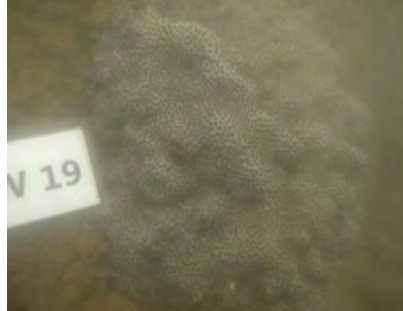

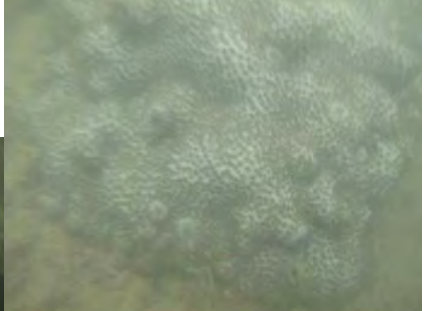



Baseline	15 th September 2011	
		
<i>11. Goniopora stutchburyi</i>		
		
<i>12. Favites pentagona</i>		
		
<i>13. Goniopora stutchburyi</i>		
		
<i>14. Porites lobata</i>		
		
<i>15. Goniastrea aspera</i>		







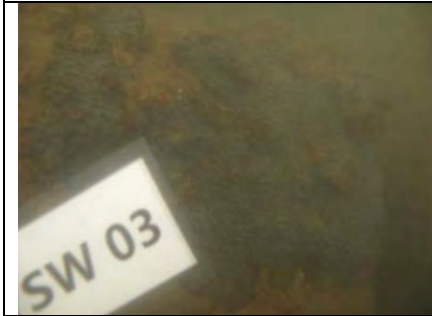








Baseline	15 th September 2011	
		
<i>16. Cyphastrea serailia</i>		
		
<i>17. Plesiastrea versipora</i>		
		
<i>18. Goniopora stutchburyi</i>		
		
<i>19. Cyphastrea serailia</i>		
		
<i>20. Porites lutea</i>		




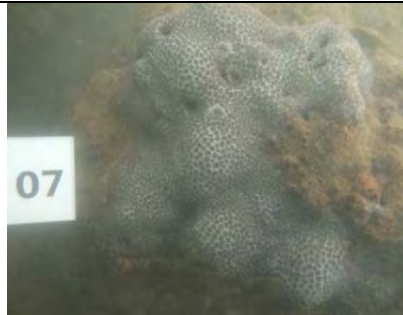











Baseline	22 nd September 2011	
		
<i>Favites chinensis</i>		
		
02. <i>Favia speciosa</i>		
		
03. <i>Favites pentagona</i>		
		
04. <i>Favia fava</i>		
		
05. <i>Porites lutea</i>		
















Baseline	22 nd September 2011	
		
<i>06. Porites lobata</i>		
		
<i>07. Cyphastrea serailia</i>		
		
<i>08. Favites chinensis</i>		
		
<i>09. Favites pentagona</i>		
		
<i>10. Coscinaraea sp.</i>		




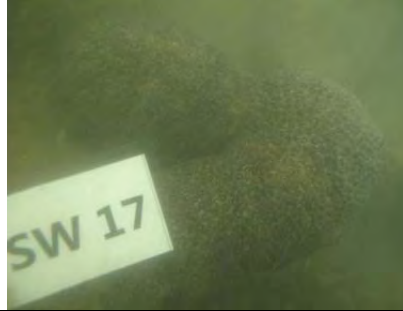





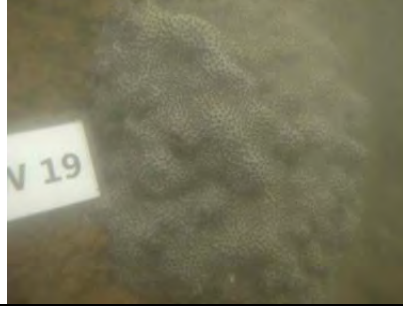

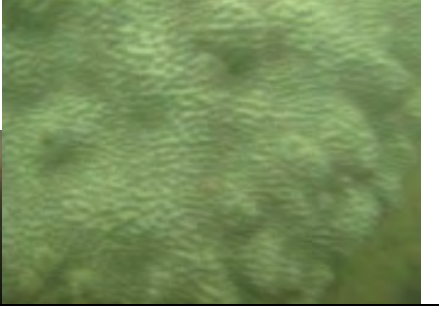



Baseline	22 nd September 2011	
		
<i>11. Goniopora stutchburyi</i>		
		
<i>12. Favites pentagona</i>		
		
<i>13. Goniopora stutchburyi</i>		
		
<i>14. Porites lobata</i>		
		
<i>15. Goniastrea aspera</i>		

Baseline	22 nd September 2011	
		
<i>16. Cyphastrea serailia</i>		
		
<i>17. Plesiastrea versipora</i>		
		
<i>18. Goniopora stutchburyi</i>		
		
<i>19. Cyphastrea serailia</i>		
		
<i>20. Porites lutea</i>		







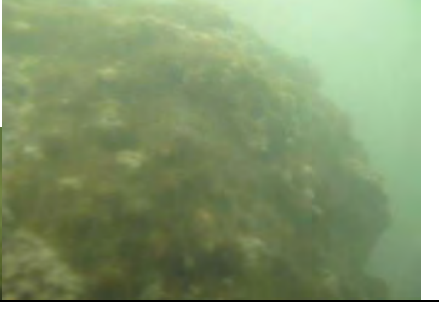





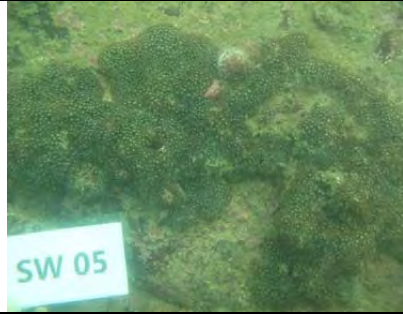


Baseline	28 th September 2011	
		
<i>Favites chinensis</i>		
		
02. <i>Favia speciosa</i>		
		
03. <i>Favites pentagona</i>		
		
04. <i>Favia fava</i>		
		
05. <i>Porites lutea</i>		



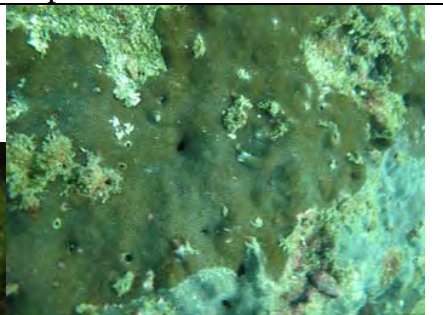
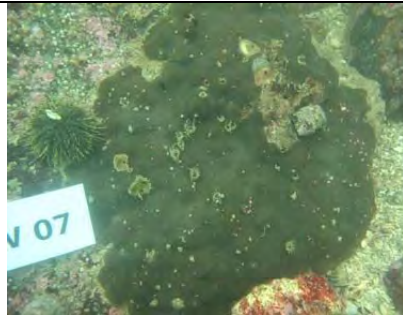

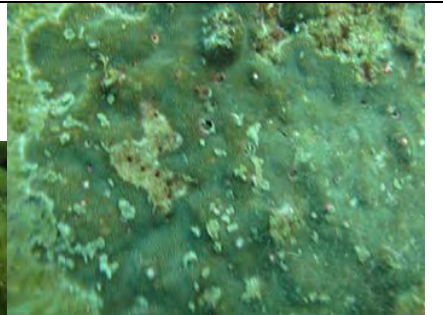
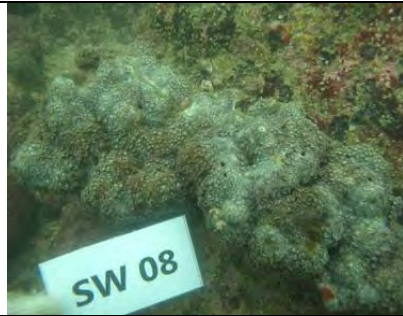


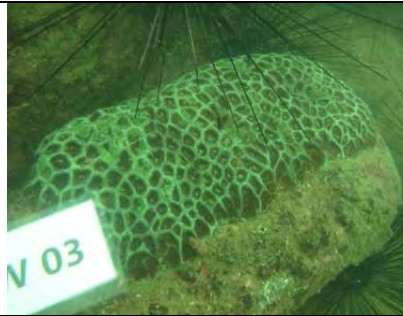


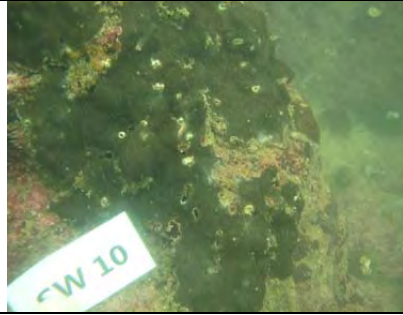

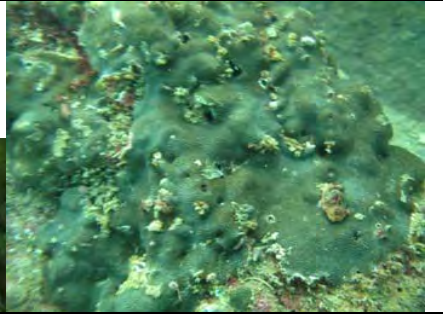
Baseline	28 th September 2011	
		
<i>06. Porites lobata</i>		
		
<i>07. Cyphastrea serailia</i>		
		
<i>08. Favites chinensis</i>		
		
<i>09. Favites pentagona</i>		
		
<i>10. Coscinaraea sp.</i>		





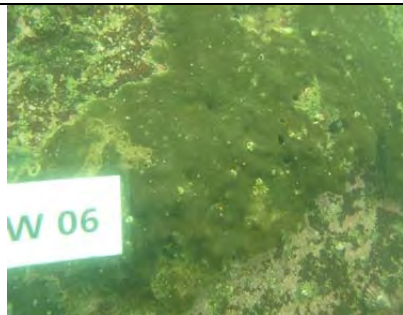










Baseline	28 th September 2011	
		
<i>11. Goniopora stutchburyi</i>		
		
<i>12. Favites pentagona</i>		
		
<i>13. Goniopora stutchburyi</i>		
		
<i>14. Porites lobata</i>		
		
<i>15. Goniastrea aspera</i>		

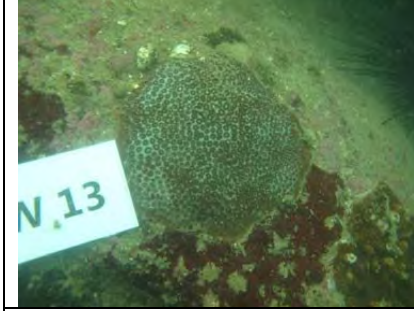











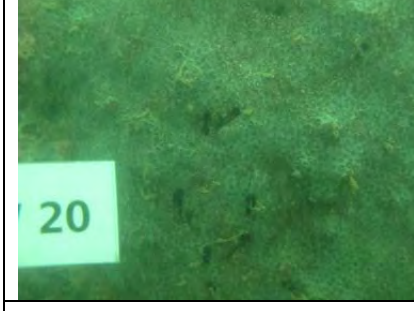


Baseline	28 th September 2011	
		
<i>16. Cyphastrea serailia</i>		
		
<i>17. Plesiastrea versipora</i>		
		
<i>18. Goniopora stutchburyi</i>		
		
<i>19. Cyphastrea serailia</i>		
		
<i>20. Porites lutea</i>		



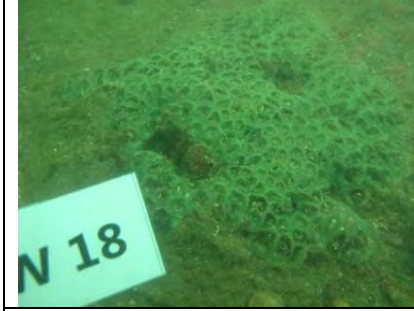









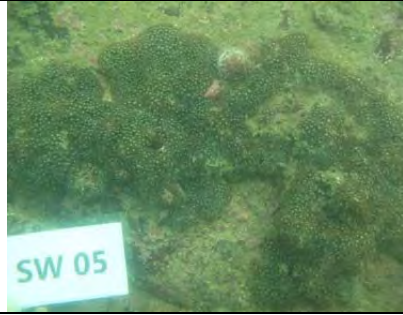

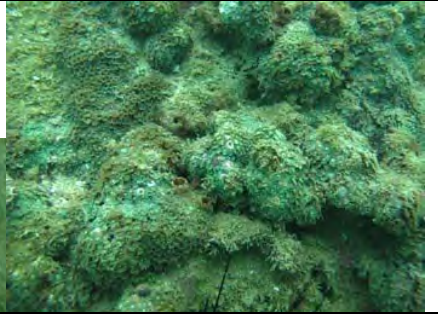
APPENDIX B Tagged Corals at Sham Wan



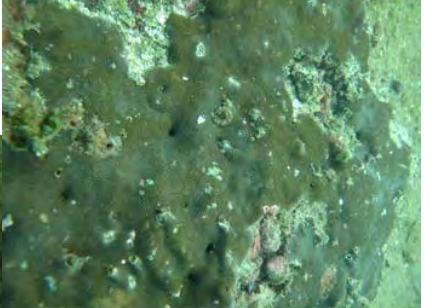




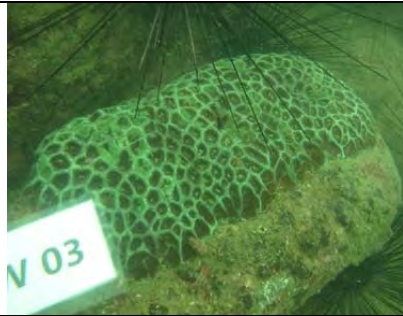




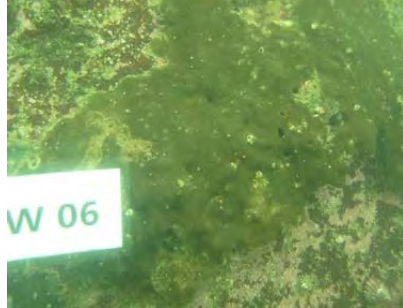


Baseline	9 th September 2011	
		
<i>01. Favia favus</i>		
		
<i>02. Favia rotumana</i>		
		
<i>03. Favia rotumana</i>		
		
<i>04. Cyphastrea serailia</i>	<i>Favia favus</i>	
		
<i>05. Goniopora stutchburyi</i>		





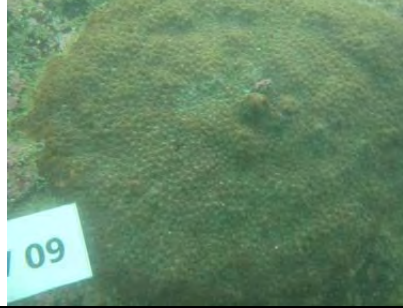

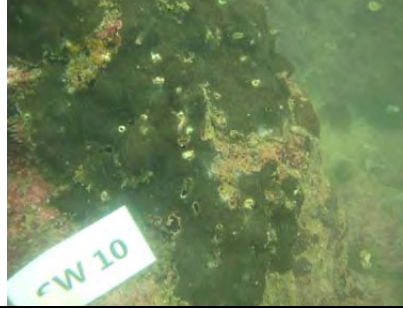








Baseline	9 th September 2011	
 <p>W 06</p>	 <p>W 06</p>	
<i>06. Porites lobata</i>		
 <p>W 07</p>	 <p>W 07</p>	
<i>07. Porites lobata</i>		
 <p>SW 08</p>	 <p>SW 08</p>	
<i>08. Goniopora stutchburyi</i>		
 <p>W 09</p>	 <p>W 09</p>	
<i>09. Favites pentagona</i>		
 <p>W 10</p>	 <p>W 10</p>	
<i>10. Porites lobata</i>		

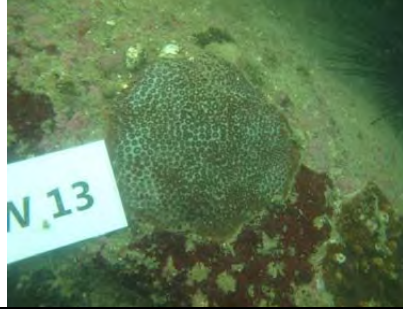











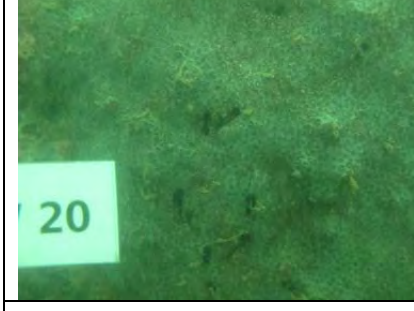


Baseline	9 th September 2011	
		
<i>11. Porites lobata</i>		
		
<i>12. Coscinaraea n sp.</i>		
		
<i>13. Cyphastrea serailia</i>		
		
<i>14. Cyphastrea serailia</i>		
		
<i>15. Favia fava</i>		



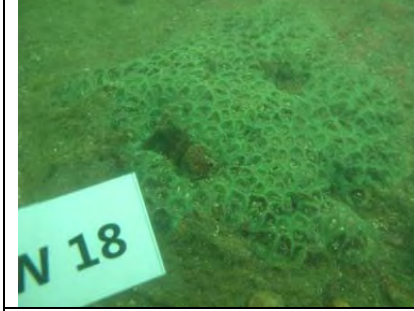











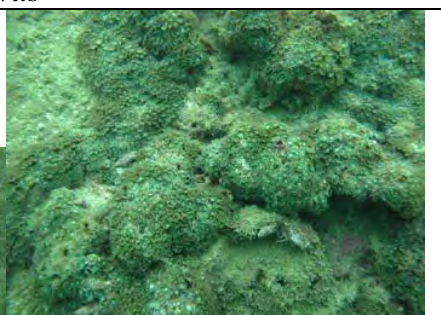
Baseline	9 th September 2011	
		
<i>16. Favia rotumana</i>		
		
<i>17. Favia favaus</i>		
		
<i>18. Favia rotumana</i>		
		
<i>19. Cyphastrea serailia</i>		
		
<i>20. Cyphastrea serailia</i>		






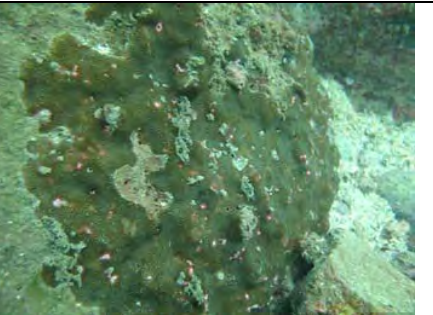
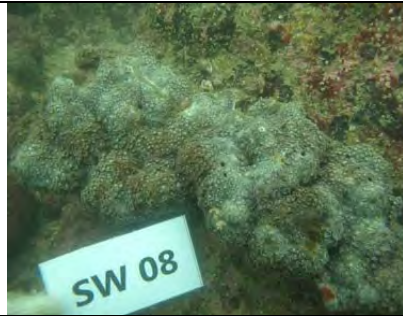





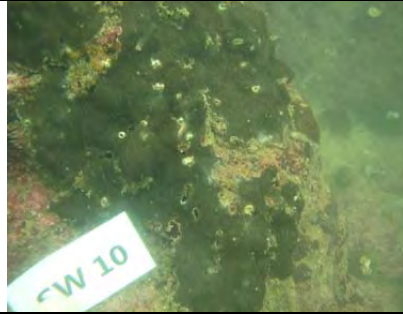

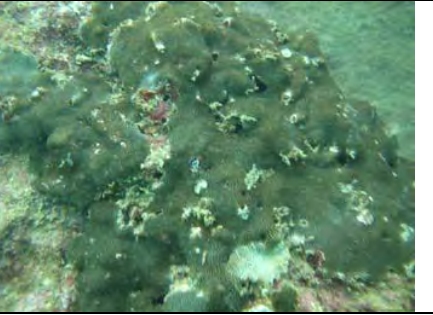
Baseline	15 th September 2011	
		
<i>01. Favia favius</i>		
		
<i>02. Favia rotumana</i>		
		
<i>03. Favia rotumana</i>		
		
<i>04. Favia favius</i>		
		
<i>05. Goniopora stutchburyi</i>		

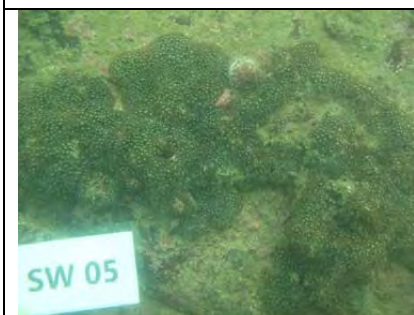

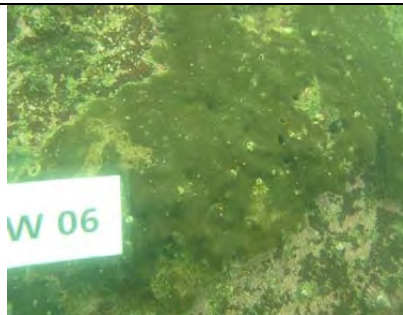

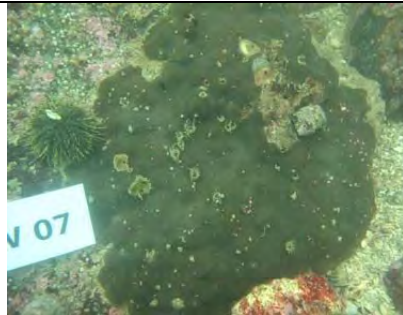



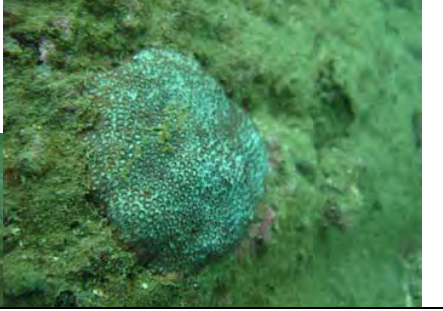






Baseline	15 th September 2011	
		
<i>06. Porites lobata</i>		
		
<i>07. Porites lobata</i>		
		
<i>08. Goniopora stutchburyi</i>		
		
<i>09. Favites pentagona</i>		
		
<i>10. Porites lobata</i>		



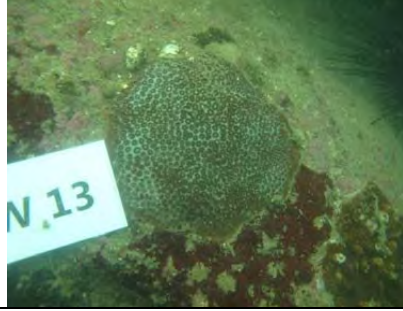












Baseline	15 th September 2011	
		
<i>11. Porites lobata</i>		
		
<i>12. Coscinaraea n sp.</i>		
		
<i>13. Cyphastrea serailia</i>		
		
<i>14. Cyphastrea serailia</i>		
		
<i>15. Favia fava</i>		

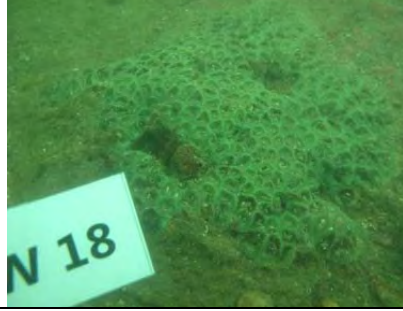














Baseline	15 th September 2011	
		
<i>16. Favia rotumana</i>		
		
<i>17. Favia fava</i>		
		
<i>18. Favia rotumana</i>		
		
<i>19. Cyphastrea serailia</i>		
		
<i>20. Cyphastrea serailia</i>		



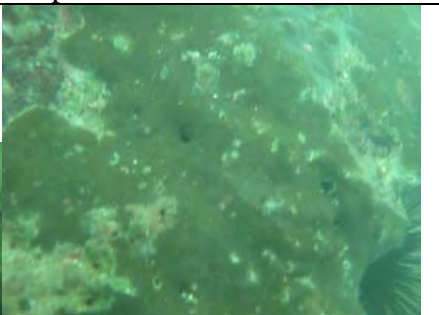
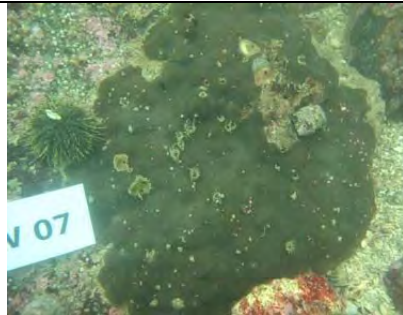

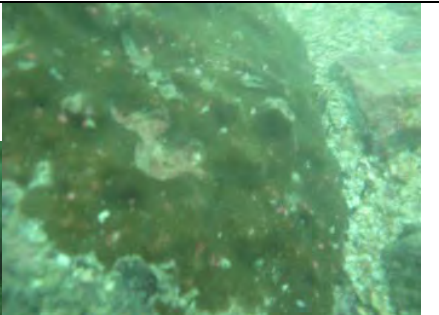
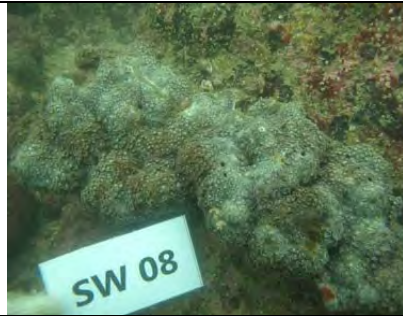


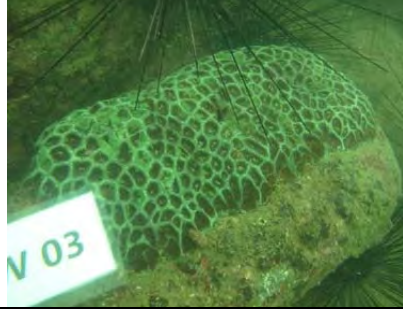


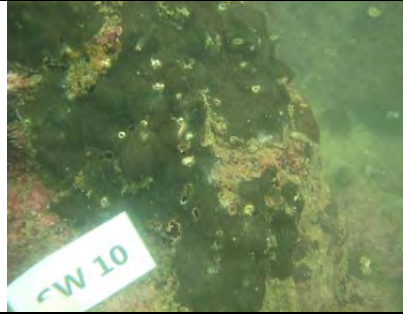


Baseline	22 th September 2011	
		
<i>01. Favia favaus</i>		
		
<i>02. Favia rotumana</i>		
		
<i>03. Favia rotumana</i>		
		
<i>04. Favia favaus</i>		
		
<i>05. Goniopora stutchburyi</i>		



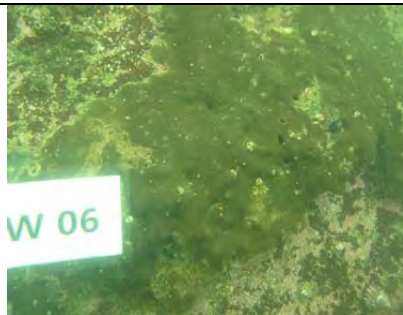


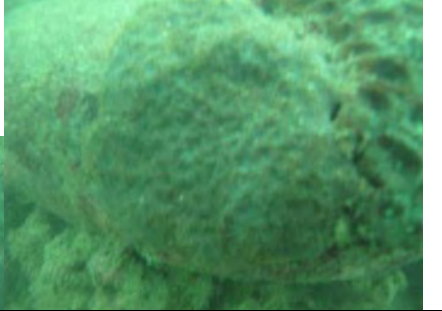
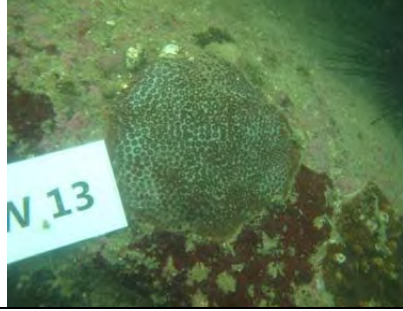








Baseline	22 th September 2011	
		
<i>06. Porites lobata</i>		
		
<i>07. Porites lobata</i>		
		
<i>08. Goniopora stutchburyi</i>		
		
<i>09. Favites pentagona</i>		
		
<i>10. Porites lobata</i>		







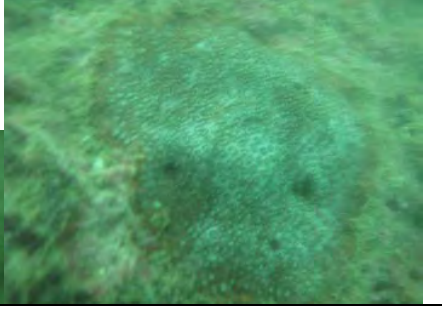








Baseline	22 th September 2011	
		
<i>11. Porites lobata</i>		
		
<i>12. Coscinaraea n sp.</i>		
		
<i>13. Cyphastrea serailia</i>		
		
<i>14. Cyphastrea serailia</i>		
		
<i>15. Favia favaus</i>		

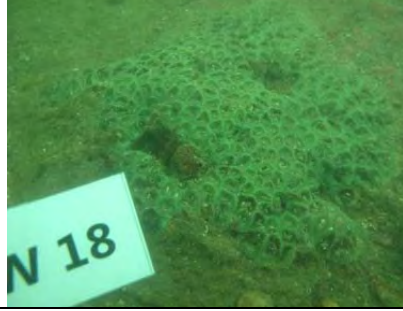Baseline	22 th September 2011	
		
<i>16. Favia rotumana</i>		
		
<i>17. Favia fava</i>		
		
<i>18. Favia rotumana</i>		
		
<i>19. Cyphastrea serailia</i>		
		
<i>20. Cyphastrea serailia</i>		

Baseline	28 th September 2011	
		
<i>01. Favia favaus</i>		
		
<i>02. Favia rotumana</i>		
		
<i>03. Favia rotumana</i>		
		
<i>04. Favia favaus</i>		
		
<i>05. Goniopora stutchburyi</i>		

Baseline	28 th September 2011	
		
<i>06. Porites lobata</i>		
		
<i>07. Porites lobata</i>		
		
<i>08. Goniopora stutchburyi</i>		
		
<i>09. Favites pentagona</i>		
		
<i>10. Porites lobata</i>		

Baseline	28 th September 2011	
		
<i>11. Porites lobata</i>		
		
<i>12. Coscinaraea n sp.</i>		
		
<i>13. Cyphastrea serailia</i>		
		
<i>14. Cyphastrea serailia</i>		
		
<i>15. Favia favaus</i>		

Baseline	28 th September 2011	
 <p data-bbox="240 405 363 488">W 16</p>	 <p data-bbox="671 405 810 488">W 16</p>	
<i>16. Favia rotumana</i>		
 <p data-bbox="240 775 363 857">N 17</p>	 <p data-bbox="671 775 794 857">N 17</p>	
<i>17. Favia favaus</i>		
 <p data-bbox="240 1128 363 1211">N 18</p>	 <p data-bbox="671 1117 794 1200">N 18</p>	
<i>18. Favia rotumana</i>		
 <p data-bbox="240 1482 363 1565">N 19</p>	 <p data-bbox="671 1471 810 1554">N 19</p>	
<i>19. Cyphastrea serailia</i>		
 <p data-bbox="240 1814 341 1897">W 20</p>	 <p data-bbox="671 1825 810 1908">W 20</p>	
<i>20. Cyphastrea serailia</i>		
