



PROJECT No.: TCS/00512/09

**DSD CONTRACT NO. DC/2009/13
CONSTRUCTION OF SEWAGE TREATMENT WORKS AT
YUNG SHUE WAN AND SOK KWU WAN**

**YUNG SHUE WAN PORTION AREA
MONTHLY ENVIRONMENTAL MONITORING AND AUDIT
(EM&A) REPORT (No.33) – MAY 2013**

PREPARED FOR
LEADER CIVIL ENGINEERING CORPORATION LIMITED

Quality Index

Date	Reference No.	Prepared By	Approved By
25 June 2013	TCS00512/09/600/R0651v3		
		Nicola Hon Environmental Consultant	T.W. Tam Environmental Team Leader

Version	Date	Description
1	18 June 2013	First Submission
2	24 June 2013	Amended against IEC's comments on 19 June 2013
3	25 June 2013	Amended against IEC's comments on 25 June 2013

URS CDM Joint Venture

Chief Engineer/Harbour Area Treatment Scheme
Drainage Services Department
5/F, Western Magistracy
2A, Pok Fu Lam Road
Hong Kong

Your reference:

Our reference: 05117/6/16/414266

Date: 25 June 2013

Attention: Ms. Jacky C M Wong


BY FAX

Dear Sirs

Contract No. DC/2009/13
Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan
Yung Shue Wan Portion Area
Monthly Environmental Monitoring and Audit (EM&A) Report No. 33 (May 2013)

We refer to the Monthly EM&A Monitoring Report No. 33 for May 2013 received under cover of the email from the Environmental Team, Action-United Environmental Services and Consulting (AUES), dated on 25 June 2013. We have no comment and have verified the captioned report.

Yours faithfully
URS CDM JOINT VENTURE



Rodney Ip
Independent Environmental Checker
ICWR/SLSY/lykl

cc Leader Civil Engineering (Attn: Mr Vincent Chan)
 AUES (Attn: Mr T.W. Tam)
 ER/LAMMA (Attn: Mr Ian Jones)
 CDM (Attn: Mr Mark Sin)

EXECUTIVE SUMMARY

ES.01. This is the 33rd monthly Environmental Monitoring and Audit (EM&A) for Yung Shue Wan (hereinafter ‘this Report’) for the designated works under Environmental Permit [EP-282/2007], covering a period from 26 April to 25 May 2013 (hereinafter ‘the Reporting Period’).

ENVIRONMENTAL MONITORING AND AUDIT ACTIVITIES

ES.02. Environmental monitoring activities under the EM&A programme in this Reporting Period are summarized in the following table.

Issues	Environmental Monitoring Parameters / Inspection	Occasions
Air Quality	1-hour TSP	30
	24-hour TSP	10
Construction Noise	$L_{eq(30min)}$ Daytime	5
Water Quality	Marine Water Sampling	12
Inspection / Audit	ET Regular Environmental Site Inspection	4

ES.03. According to the construction information provided by the Contractor, the marine works in Yung Shue Wan has been completed on 22 April 2013. In this Reporting Period, as agreed by the Contractor, the ecology monitoring was ceased due to no ecological impact and concern since the completion of marine work, whereas impact marine water quality monitoring would be ongoing until further notice. The corresponding letter regards to the completion of marine work in Yung Shue Wan issued by the Contractor is presented in Appendix M.

BREACH OF ACTION AND LIMIT (A/L) LEVELS

ES.04. No exceedance in air quality and construction noise monitoring was recorded in this Reporting Period. The statistics of environmental exceedance, NOE issued and investigation of exceedance are summarized in the following table.

Environmental Issues	Monitoring Parameters	Action Level	Limit Level	Event & Action		
				NOE Issued	Investigation	Corrective Actions
Air Quality	1-hour TSP	0	0	0	--	--
	24-hour TSP	0	0	0	--	--
Construction Noise	$L_{eq(30min)}$ Daytime	0	0	0	--	--
Water Quality	DO	0	0	0	--	--
	Turbidity	0	0	0	--	--
	SS	0	0	0	--	--
Ecology (Coral)	Sediment Cover (%)	--	--	--	--	--
	Bleaching (%)	--	--	--	--	--
	Mortality (%)	--	--	--	--	--

Note: NOE – Notification of Exceedance

SITE INSPECTION

ES.05. In this Reporting Period, 4 events of weekly joint inspection by the RE, the Contractor and ET were carried out on 30 April, 7, 14 and 21 May 2013.

ENVIRONMENTAL COMPLAINT, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

ES.06. No written or verbal complaint, environmental summons or successful prosecutions were recorded in this Reporting Period.

REPORTING CHANGE

ES.07. In this Reporting Period, as agreed by the Contractor, the ecology monitoring was ceased since

the completion of marine work on 22 April 2013. The corresponding letter regards to the completion of marine work in Yung Shue Wan issued by the Contractor is presented in Appendix M.

FUTURE KEY ISSUES

- ES.08. During wet season, the Contractor shall pay attention on the potential water impact as the construction site is adjacent to the coastline. Muddy water and other water quality pollutants via site surface water runoff into the coral zones of Yung Shue Wan seawall, Shek Kok Tsui and O Tsai should be avoided. Mitigation measures for water quality should be fully implemented.
- ES.09. Nevertheless, the Contractor shall keep paying attention on the potential water impact as the construction site is adjacent to the coastline. Muddy water and other water quality pollutants via site surface water runoff into the sea body within Fish culture zone at Picnic Bay and the Secondary recreation contact subzone at Mo Tat Wan should be avoided. Therefore, mitigation measures for water quality should be fully implemented.

TABLE OF CONTENTS

1	INTRODUCTION	1
	PROJECT BACKGROUND	1
	REPORT STRUCTURE	1
2	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS	2
	PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE	2
	CONSTRUCTION PROGRESS	2
	SUMMARY OF ENVIRONMENTAL SUBMISSIONS	2
3	SUMMARY OF BASELINE MONITORING REQUIREMENTS	4
	ENVIRONMENTAL ASPECT	4
	MONITORING LOCATIONS	4
	MONITORING FREQUENCY AND PERIOD	5
	MONITORING EQUIPMENT	6
	EQUIPMENT CALIBRATION	7
	METEOROLOGICAL INFORMATION	8
	DATA MANAGEMENT AND DATA QA/QC CONTROL	8
	REPORTING	8
	DETERMINATION OF ACTION/LIMIT (A/L) LEVELS	8
4	IMPACT MONITORING RESULTS - AIR QUALITY	10
5	IMPACT MONITORING RESULTS – CONSTRUCTION NOISE	11
6	IMPACT MONITORING RESULTS – WATER QUALITY	12
7	IMPACT MONITORING RESULTS – ECOLOGY MONITORING	14
8	WASTE MANAGEMENT	15
9	SITE INSPECTION	16
10	ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE	17
11	IMPLEMENTATION STATUS OF MITIGATION MEASURES	18
12	IMPACT FORECAST	24
13	CONCLUSIONS AND RECOMMENDATIONS	25
	CONCLUSIONS	25
	RECOMMENDATIONS	25

LIST OF TABLES

Table 2-1	Status of Environmental Licenses and Permits
Table 2-2	Status of EM&A Programme Submission
Table 3-1	Summary of EM&A Requirements
Table 3-2	Location of Air Quality Monitoring Station
Table 3-3	Location of Construction Noise Monitoring Station
Table 3-4	Location of Marine Water Quality Monitoring Station
Table 3-5	Action and Limit Levels for Air Quality
Table 3-6	Action and Limit Levels for Construction Noise
Table 3-7	Action and Limit Levels for Marine Water Quality
Table 3-8	Action and Limit Levels for Coral Monitoring
Table 4-1	Summary of 24-hour and 1-hour TSP Monitoring Results at AC02b
Table 4-2	Summary of 24-hour and 1-hour TSP Monitoring Results at AC04c
Table 5-1	Summarized of Construction Noise Monitoring Results at NC05
Table 6-1	Summary of Water Quality Results – Mid-ebb Tides (Dissolved Oxygen)
Table 6-2	Summary of Water Quality Results – Mid-ebb Tides (Turbidity & Suspended Solids)
Table 6-3	Summary of Water Quality Results – Mid-flood Tides (Dissolved Oxygen)
Table 6-4	Summary of Water Quality Results – Mid-flood Tides (Turbidity & Suspended Solids)
Table 6-5	Summarized Exceedances of Marine Water Quality
Table 8-1	Summary of Quantities of Inert C&D Materials
Table 8-2	Summary of Quantities of C&D Wastes
Table 9-1	Site Observations
Table 10-1	Statistical Summary of Environmental Complaints
Table 10-2	Statistical Summary of Environmental Summons
Table 10-3	Statistical Summary of Environmental Prosecution
Table 11-1	Environmental Mitigation Measures

LIST OF APPENDICES

Appendix A	Site Layout Plan – Yung Shue Wan Portion Area
Appendix B	Organization Structure and Contact Details of Relevant Parties
Appendix C	Master and Three Months Rolling Construction Programme
Appendix D	Location of Monitoring Stations (Air Quality / Construction Noise / Water Quality/ Dive Surveys of Coral)
Appendix E	Monitoring Equipments Calibration Certificate
Appendix F	Event and Action Plan
Appendix G	Monitoring Data Sheet
Appendix H	Graphical Plots of Monitoring Results
Appendix I	Meteorological Information
Appendix J	Monthly Summary Waste Flow Table
Appendix K	Weekly Site Inspection Checklist
Appendix L	Implementation Schedule of Mitigation Measures
Appendix M	Corresponding Letter

1 INTRODUCTION

PROJECT BACKGROUND

- 1.01 The Leader Civil Engineering Corporation Limited (Leader) has been awarded the *Contract DC/2009/13 - Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan* (the Project) by the Drainage Services Department (DSD) on 4 May 2010. The Project is part of an overall plan approved under a statutory EIA for Outlying Islands Sewerage Stage 1 Phase 2 Package J – Sok Kwu Wan Sewage Collection and Treatment (Register No. AEIAR-075/2003) and Disposal Facilities and Outlying Islands Sewerage Stage 1 Phase 1 Package C – Yung Shue Wan Sewage Treatment Works and Outfall (Register No. EIA-124/BC). The Environmental Permit (EP) No. EP-281/2007 and EP-282/2007 for the Project have been obtained by the DSD on 29 June 2007 for the relevant works. After July 2009, EP-281/2007/A instead EP-281/2007 is EP for Sok Kwu Wan relevant Works.
- 1.02 The Project involves construction of sewage treatment works at Sok Kwu Wan and Yung Shue Wan with a capacity of 1,430m³/day and 2,850m³/day respectively to provide secondary treatment, construction of 2 pumping stations at Sok Kwu Wan and 1 pumping station at Yung Shue Wan, construction of submarine outfall from the coastline and laying of underground sewerage pipeline. The site layout plan for the captioned work under the Project is showing in **Appendix A**
- 1.03 According to the Particular Specification (PS) and **Appendix 25** of the Project, Leader should establish an Environmental Team (ET) to implement the environmental monitoring and auditing works to fulfill the requirements as stipulated in the EM&A Manual. This EM&A Manual is referred to the Appendix D of the Review Report on EIA Study – Yung Shue Wan (Final) in January 2007 (Agreement No. CE 20/2005(DS)).
- 1.04 Action-United Environmental Services and Consulting (AUES) has been commissioned by Leader as the ET to implement the relevant EM&A programme. Organization chart of the Environmental Team for the Project is shown in **Appendix B**. For ease of reporting, the proposed EM&A programme for baseline and impact monitoring is split to following two stand-alone parts:
- (a) Proposed EM&A Programme for Baseline and Impact Monitoring – Sok Kwu Wan (under EP No. 281/2007/A varied on 23 September 2009)
- (b) Proposed EM&A Programme for Baseline and Impact Monitoring – Yung Shue Wan (under EP No. 282/2007)
- 1.05 This is the 33rd monthly EM&A Report for Yung Shue Wan Portion Area which presenting the monitoring results and inspection findings in the Reporting Period from **26 April to 25 May 2013**.

REPORT STRUCTURE

- 1.06 The Monthly Environmental Monitoring and Audit (EM&A) Report – Yung Shue Wan is structured into the following sections:-

SECTION 1	INTRODUCTION
SECTION 2	PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS
SECTION 3	SUMMARY OF MONITORING REQUIREMENTS
SECTION 4	AIR QUALITY MONITORING RESULTS
SECTION 5	CONSTRUCTION NOISE MONITORING RESULTS
SECTION 6	WATER QUALITY MONITORING RESULTS
SECTION 7	ECOLOGY MONITORING RESULTS
SECTION 8	WASTE MANAGEMENT
SECTION 9	SITE INSPECTIONS
SECTION 10	ENVIRONMENTAL COMPLAINTS AND NON-COMPLIANCE
SECTION 11	IMPLEMENTATION STATUES OF MITIGATION MEASURES
SECTION 12	IMPACT FORECAST
SECTION 13	CONCLUSIONS AND RECOMMENDATION

2 PROJECT ORGANIZATION AND CONSTRUCTION PROGRESS

PROJECT ORGANIZATION AND MANAGEMENT STRUCTURE

- 2.01 Organization structure and contact details of relevant parties with respect to on-site environmental management are shown in [Appendix B](#).

CONSTRUCTION PROGRESS

- 2.02 The master and three month rolling construction programme are enclosed in [Appendix C](#) and the major construction activities undertaken in this Reporting Period are listed below:-
- Construction of road and drainage works in yard area
 - Casting Concrete for the FS tank,
 - Excavation and lateral support for HEC Cable Trench,
 - Rebar fixing, formwork erection/ removal
 - Backfilling and soil compaction
 - E&M installation
 - Plumb and Drain installation
 - Plastering and painting
 - Casting concrete for floor finishing,
 - Installation of doors and FRP cover

SUMMARY OF ENVIRONMENTAL SUBMISSIONS

- 2.03 Summary of the relevant permits, licences, and/or notifications on environmental protection for this Project in this Reporting Period is presented in [Table 2-1](#).

Table 2-1 Status of Environmental Licenses and Permits

Item	Description	License/Permit Status
1	Air Pollution Control (Construction Dust) Regulation	Notified 19/5/2010 Case No: 317486
2	Chemical Waste Producer Registration	Issued on 8/6/2010 WPN 5213-912-L2720-01
3	Water Pollution Control Ordinance	Issued on 22/9/2010 WT00007566-2010
4	Billing Account for Disposal of Construction Waste	Issued on 26 May 2010 A/C No: 7010815
5	Construction Noise Permit (no. GW-RS0074-13)	Issued on 29 January 2013 Valid from 29 January 2013 until 25 July 2013

- 2.04 Summary of the report submission for EM&A Programme is presented in [Table 2-2](#).

Table 2-2 Status of EM&A Programme Submission

Item	EM&A Programme Submission	Status
1	Proposed EM&A Programme for Baseline / Impact Monitoring – Yung Shue Wan (TCS00512/09/600/R0011 Ver.5)	Verified by IEC and submitted to EPD on 8 July 2010
2	Method Statement for Coral Monitoring – Yung Shue Wan (TCS00512/09/600/R0071 Ver.3)	Verified by IEC and submitted to EPD on 25 November 2010
3	Baseline Air and Noise Monitoring Report - Volume 1 (TCS00512/09/600/R0061 Ver.3)	Verified by IEC and submitted to EPD on 31 August 2010
4	Baseline Monitoring Report Volume 2 - Water Quality (TCS00512/09/600/R0158 Ver.2)	Verified by IEC and submitted to EPD on 10 March 2011
5	Baseline Survey for Coral Monitoring – Yung Shue Wan (TCS00512/09/600/R0132 Ver.3)	Verified by IEC and submitted to EPD on 17 February 2011

Item	EM&A Programme Submission	Status
6	Methodology of Coral Tagging for Impact Monitoring – Yung Shue Wan	Verified by IEC and submitted to EPD on 28 March 2011
7	Coral Tagging Report (TCS00512/09/600/R0214Ver.4)	Verified by IEC and submitted to EPD on 3 August 2011

3 SUMMARY OF BASELINE MONITORING REQUIREMENTS

ENVIRONMENTAL ASPECT

- 3.01 The EM&A baseline monitoring programme cover the following environmental issues:
- Air quality;
 - Construction noise;
 - Marine water quality; and
 - Ecology monitoring
- 3.02 The ET implements the EM&A programme in accordance with the aforementioned requirements. Detailed air quality, construction noise, water quality and ecology of the EM&A programme are presented in the following sub-sections.
- 3.03 A summary of the air, noise, marine water and ecology monitoring parameters is presented in **Table 3-1**:

Table 3-1 Summary of the EM&A Requirements

Environmental Issue	Parameters
Air Quality	<ul style="list-style-type: none"> • 1-hour TSP Monitoring by Real-Time Portable Dust Meter; and • 24-hour TSP Monitoring by High Volume Air Sampler.
Noise	<ul style="list-style-type: none"> • $L_{eq(30min)}$ during normal working hours; and • $L_{eq(15min)}$ during Restricted Hours.
Marine Water Quality	<p><i>In-situ Measurements</i></p> <ul style="list-style-type: none"> • Dissolved Oxygen Concentration (DO) (mg/L); • Dissolved Oxygen Saturation (%); • Turbidity (NTU); • pH unit; • Salinity (ppt); • Water depth (m); and • Temperature (°C). <p><i>Laboratory Analysis</i></p> <ul style="list-style-type: none"> • Suspended Solids (SS) (mg/L)
Ecology	<ul style="list-style-type: none"> • Coral Monitoring

MONITORING LOCATIONS

Air Quality

- 3.04 Two designated monitoring stations, AC02a located at Yung Shue Wan Refuse Transfer Station and AC04 located at residential area nearby Yung Shue Wan football pitch, were recommended in the *EM&A Manual Section 2.5*. In order to identify and seek for the access of the air monitoring locations designated in the EM&A Manual, site visit was conducted by Leader and ET.
- 3.05 At the site visit, all designated monitoring locations were identified however the premises for high volume sampler installation were objected by the owner or the residents of nearby. So, alternative air monitoring locations were proposed in accordance with the criteria set out in *EM&A manual Section 2.5.2 and 2.5.3*. The proposed alternative air monitoring stations were accepted by the Engineer Representative (ER) and Independent Environmental Checker (IEC) and EPD for endorsement. Details of renewed air monitoring stations are described in **Table 3-2**. The graphical of air monitoring stations is shown in **Appendix D**.

Table 3-2 Location of Air Quality Monitoring Station

Sensitive Receiver	Location
AC02b	The entrance of RE's site office
AC04c	Next to a power transformer station TP208 Yung Shue Wan and adjacent to the road direct to the construction site

Construction Noise

- 3.06 According to *EM&A Manual Section 3.4*, one noise sensitive receivers (NC05) designated for the construction noise monitoring was recommended at Yung Shue Wan Portion Area of the Project. The designated monitoring station is identified and successfully granted the premises. The detailed construction noise monitoring station is described in *Table 3-3* and graphical is shown in *Appendix D*.

Table 3-3 Location of Construction Noise Monitoring Station

Sensitive Receiver	Location
NC05	Roof of North Lamma Clinic

Marine Water Quality

- 3.07 Two control stations (CY1 and CY2) and three impact stations (WY1-WY3) were recommended in the *EM&A Manual Section 4.5*. Impact stations WY1-WY3 were identified close to the sensitive receivers (the coral colonies in the vicinity of Yung Shue Wan, and secondary contact recreation subzone). It is proposed to monitor the impacts from the construction of the submarine outfall as well as the effluent discharge from the proposed STW on water quality. Two control stations: CY1 and CY2 were recommended at locations representative of the project site in its undisturbed condition and located at upstream and downstream of the works area. The marine water quality monitoring stations to be performed under the Project is described in *Table 3-4* and shown in *Appendix D*.

Table 3-4 Location of Marine Water Quality Monitoring Station

Station	Description	Coordinates	
		Easting	Northing
WY1	Coral colonies on seawall at STW site	829 170	809 550
WY2	Coral colonies at Shek kok Tsui	829 000	810 400
WY3	Coral colonies at O Tsai (headland N at SW ferry pier)	829 200	809 850
CY1 (flood)	Control Station	828 400	810 800
CY2 (ebb)	Control Station	828 000	808 800

Coral Monitoring

- 3.08 The coral monitoring stations to be performed under the Project is show in *Appendix D*. The ecology monitoring was ceased since the completion of marine work on 22 April 2013. The corresponding letter regards to the completion of marine work in Yung Shue Wan issued by the Contractor is presented in Appendix M.

MONITORING FREQUENCY AND PERIOD

- 3.09 The Impact monitoring carried out in the EM&A programme is basically in accordance with the requirements in *EM&A Manual Sections 2.7, 3.6, 4.7, 4.8, 7.3 and 7.4*. The monitoring requirements are listed as follows:

Air Quality Monitoring

Parameters: 1-hour TSP and 24-hour TSP

Frequency: Once in every six days for 24-hour TSP and three times in every six days for 1-hour TSP

Duration: Throughout the construction period

Noise Monitoring

Parameters: $L_{eq(30min)}$ & $L_{eq(5min)}$, L_{10} and L_{90} .

$L_{eq(15min)}$ & $L_{eq(5min)}$, L_{10} and L_{90} during the construction undertaken during Restricted hours (19:00 to 07:00 hours next of normal working day and full day of public holiday and Sunday)

Frequency: Once per week during 0700-1900 hours on normal weekdays. Restricted hour monitoring should depend on conditions stipulated in Construction Noise Permit

Duration: Throughout the construction period

Marine Water Quality Monitoring

Parameters: Duplicate in-situ measurements: water depth, temperature, dissolved oxygen, pH, turbidity and salinity
HOKLAS-accredited laboratory analysis: suspended solids

Frequency: Three days a week, at mid ebb and mid flood tides. The interval between 2 sets of monitoring will be more than 36 hours

Sampling Depth (i.) Three depths: 1m below water surface, 1m above sea bottom and at mid-depth when the water depth exceeds 6m.
(ii.) If the water depth is between 3m and 6m, two depths: 1m below water surface and 1m above sea bottom
(iii.) If the water depth is less than 3m, 1 sample at mid-depth is taken

Duration: During the course of marine works

Coral Monitoring

Parameters: Presence and coverage of hard and soft corals such as diversity, abundance and health status of the corals in the general area, plus other physical and biological condition at the underwater environment

Frequency: One per week for the first three months of the marine works. If no exceedances are reported during the first three months, the frequency may be reduced to twice every month

Duration: During the course of marine works

Post-Construction Monitoring – Marine Water

- 3.10 Upon the marine works (dredging and HDD pipe installation) completion, 4 weeks of post-construction monitoring would be undertaken in accordance with the *Section 4.8 of EM&A Manual*. The requirements of post-construction monitoring such as the parameter, frequency, location and sampling depth is same as the impact monitoring.

Post-Construction Monitoring – Ecology Monitoring

- 3.11 Following completion of the marine works, post project monitoring should be carried out within two weeks of completion of the marine works (HDD and dredging), and should comprise the same two-tier Rapid Assessment Ecological Assessment (REA) method adopted for the baseline survey.

MONITORING EQUIPMENT

Air Quality Monitoring

- 3.12 The 24-hour and 1-hour TSP levels shall be measured by following the standard high volume sampling method as set out in the *Title 40 of the Code of Federal Regulations, Chapter 1 (Part 50), Appendix B*. If the ET proposes to use a direct reading dust meter to measure 1-hour TSP levels, it shall submit sufficient information to the IEC to approve. The filter paper of 24-hour TSP measurement shall be determined by HOKLAS accredited laboratory.

Noise Monitoring

- 3.13 Sound level meter in compliance with the *International Electrotechnical Commission Publications 651: 1979 (Type 1) and 804: 1985 (Type 1)* specifications shall be used for carrying out the noise monitoring. The sound level meter shall be checked using an acoustic calibrator. The wind speed shall be checked with a portable wind speed meter capable of measuring the

wind speed in m/s.

Water Quality Monitoring

- 3.14 **Dissolved Oxygen and Temperature Measuring Equipment** – The instrument should be a portable and weatherproof dissolved oxygen (DO) measuring instrument complete with cable and sensor, and use a DC power source. The equipment should be capable of measuring as included a DO level in the range of 0 – 20mg L⁻¹ and 0 – 200% saturation; and a temperature of 0 – 45 degree Celsius.
- 3.15 **pH Meter** – The instrument shall consist of a potentiometer, a glass electrode, a reference electrode and a temperature-compensating device. It shall be readable to 0.1 pH in arrange of 0 to 14.
- 3.16 **Turbidity (NTU) Measuring Equipment** – The instrument should be a portable and weatherproof turbidity measuring instrument using a DC power source. It should have a photoelectric sensor capable of measuring turbidity between 0 - 1000 NTU.
- 3.17 **Water Sampling Equipment** – A water sampler should comprise a transparent PVC cylinder, with a capacity of not less than 2 litres, which can be effectively sealed with latex cups at both ends. The sampler should have a positive latching system to keep it open and prevent premature closure until released by a messenger when the sampler is at the selected water depth.
- 3.18 **Water Depth Detector** – A portable, battery-operated echo sounder should be used for the determination of water depth at each designated monitoring station. This unit can either be hand held or affixed to the bottom of the work boat.
- 3.19 **Salinity Measuring Equipment** – A portable salinometer capable of measuring salinity in the range of 0 - 40 parts per thousand (ppt) should be provided for measuring salinity of the water at each monitoring location.
- 3.20 **Sample Containers and Storage** – Water samples for suspended solids should be stored in high density polythene bottles with no preservative added, packed in ice (cooled to 4°C without being frozen).
- 3.21 **Monitoring Position Equipment** - A hand-held or boat-fixed type digital Differential Global Positioning System (DGPS) with way point bearing indication and Radio Technical Commission for maritime (RTCM) Type 16 error message ‘screen pop-up’ facilities (for real-time auto-display of error messages and DGPS corrections from the Hong Kong Hydrographic Office), or other equipment instrument of similar accuracy, should be provided and used during marine water monitoring to ensure the monitoring vessel is at the correct location before taking measurements.
- 3.22 **Suspended Solids Analysis** – Analysis of suspended solids shall be carried out in a HOKLAS or other international accredited laboratory.

Coral Monitoring

- 3.23 The monitoring equipments used for the coral monitoring could be referred to **Impact Coral Monitoring report** which enclosed in [Appendix M](#).

EQUIPMENT CALIBRATION

- 3.24 Calibration of the High Volume Sampler (HVS) is performed upon installation in accordance with the manufacturer’s instruction using the NIST-certified standard calibrator (Tisch Calibration Kit Model TE-5025A). The calibration data are properly documented and the records are maintained by ET for future reference.
- 3.25 The 1-hour TSP meter was calibrated by the supplier prior to purchase. Zero response of the equipment was checked before and after each monitoring event. In-house calibration with the

High Volume Sampler (HVS) in same condition was undertaken in yearly basis.

- 3.26 The sound level meter and calibrator are calibrated and certified by a laboratory accredited under HOKLAS or any other international accreditation scheme at yearly basis.
- 3.27 The water quality monitoring equipments such as DO meter, pH Meter, turbidity measuring instrument and salinometer, are calibrated by HOKLAS accredited laboratory of three month intervals.
- 3.28 All updated calibration certificates of the monitoring equipment used for the impact monitoring programme in the Reporting Period would be attached in *Appendix E*.

METEOROLOGICAL INFORMATION

- 3.29 The meteorological information during the construction phase is obtained from the Wong Chuk Hang Station of the Hong Kong Observatory (HKO) due to it nearly the Project site.

DATA MANAGEMENT AND DATA QA/QC CONTROL

- 3.30 The impact monitoring data are handled by the ET’s systematic data recording and management, which complies with in-house Quality Management System. Standard Field Data Sheets (FDS) are used in the impact monitoring programme.
- 3.31 The monitoring data recorded in the equipment e.g. 1-hour TSP meter, sound level meter and Multi-parameter Water Quality Monitoring System, are downloaded directly from the equipments at the end of each monitoring day. The downloaded monitoring data are input into a computerized database properly maintained by the ET. The laboratory results are input directly into the computerized database and QA/QC checked by personnel other than those who input the data. For monitoring activities require laboratory analysis, the local laboratory follows the QA/QC requirements as set out under the HOKLAS scheme for all laboratory testing.

REPORTING

- 3.32 It was agreed among the ER, IEC, Contractor and ET that, in order to streamline the EM&A report submission and to cater for the occasional delay in obtaining laboratory analysis results, the cutoff day for each month is the 25th i.e. the first day of each report is the 26th of the last month and the end day, the 25th of that month.

DETERMINATION OF ACTION/LIMIT (A/L) LEVELS

- 3.33 According to the Yung Shue Wan Environmental Monitoring and Audit Manual, the air quality, construction noise, marine water quality and coral monitoring were established, namely Action and Limit levels are listed in *Tables 3-5 to 3-8* as below.

Table 3-5 Action and Limit Levels for Air Quality

Monitoring Station	Action Level (µg /m ³)		Limit Level (µg/m ³)	
	1-hour TSP	24-hour TSP	1-hour TSP	24-hour TSP
AC02b	288	161	500	260
AC04c	290	176	500	260

Table 3-6 Action and Limit Levels for Construction Noise

Recommended Action & Limit Levels of Construction Noise		
Monitoring Location	Action Level	Limit Level
	0700-1900 hours on normal weekdays	
NC05	When one or more documented complaints are received	75 dB(A) *

Note: * Reduces to 70dB(A) for schools and 65dB(A) during the school examination periods.

Table 3-7 Action and Limit Levels for Marine Water Quality

Parameter	Performance Criteria	Impact Station		
		WY1	WY2	WY3
DO Concentration (Surface and Middle) (mg/L)	Action Level	3.63	3.53	3.61
	Limit Level	3.32	3.47	3.42
DO Concentration (Bottom) (mg/L)	Action Level	3.33	2.92	3.36
	Limit Level	3.23	2.63	3.14
Turbidity (Depth-Average) (NTU)	Action Level	10.94	14.16	14.99
	Limit Level	17.35	15.20	16.21
Suspended Solids (Depth-Average) (mg/L)	Action Level	17.52	14.04	14.52
	Limit Level	25.62	16.51	16.88

Table 3-8 Action and Limit Levels for Coral Monitoring

Step	Action
1	Commence tagged coral monitoring at the impact site. If no increase in sedimentation cover/bleaching/partial mortality is observed on the hard corals or partial mortality on the soft/black corals, no action is required. If an increase in sedimentation cover/bleaching/partial mortality is observed on the hard corals or partial mortality on the soft/black corals at one or more impact monitoring stations Step 3 should be enacted, if not, Step 2.
2	If non actions are triggered a formal report should be issued along with evidentiary photographs following completion of the survey. Meanwhile monitoring work and construction works should continue uninterrupted.
3	If during the impact monitoring a 15% increase in the percentage of sedimentation on the hard corals occurs at more than 20% of the tagged coral colonies at the Impact Monitoring Station that is not reported at the Control Monitoring Station, then the Action Level is exceeded (Step 4).
4	If the Action Level is exceeded the IC(E) should inform all parties. The data from the water quality monitoring should also be reviewed. If the water quality monitoring shows no attributable effects of the installation works, then the Action Level is not triggered. If the water quality data indicate exceedances (for SS and/or turbidity) the IC(E) should discuss with the Contractor the most appropriate method of reducing suspended solids during construction (e.g. reduce rate of dredging). The water quality data reviewed should then be enacted on the next working day.
5	Monitoring should proceed the following day as per Step 1. If during the Impact Monitoring a 25% increase in the percentage of sedimentation on the hard corals at more than 20% of the tagged coral colonies at the Impact Monitoring Station that is not reported at the Control Monitoring Station, then the Limit Level is exceeded (Step 6). If the Limit Level is not exceeded Step 2 is enacted and work continues according to the mitigated method.
6	If the Limit Level is exceeded the Inspector Officer should inform all parties immediately. Should the Limit Level be exceeded, the Contractor should stop works immediately and work out a solution to the satisfaction of the IC(E), EPD and AFCD. The IC(E) should inform the Contractor to suspend marine construction works until an effective solution is identified. Once the solution has identified and agreed with all parties, backfilling works may re-commence.

3.34 Should non-compliance of the environmental quality criteria occurs, remedial actions will be triggered according to the Event and Action Plan enclosed in [Appendix F](#).

4 IMPACT MONITORING RESULTS - AIR QUALITY

4.01 As informed by the Contractor, the construction of relevant land works at Yung Shue Wan was commenced on 14 September 2010. The impact EM&A programme was begun as compliance with the contract Particular Specification, Yung Shue Wan EM&A Manual and the EP.

Result

4.02 In this Reporting Period, the results for 24-hour and 1-hour TSP monitoring are tabulated in *Tables 4-1 and 4-2*. The 24-hour TSP monitoring data are shown in *Appendix G* and the graphical plots are shown in *Appendix H*.

Table 4-1 Summary of 24-hour and 1-hour TSP Monitoring Results at AC02b

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st hour measured	2 nd hour measured	3 rd hour measured
2-May-13	103	30-Apr-13	11:19	134	126	135
8-May-13	25	6-May-13	12:15	142	158	144
14-May-13	94	10-May-13	10:35	146	149	137
20-May-13	34	16-May-13	10:03	122	129	116
25-May-13	31	22-May-13	10:30	69	74	66
Average (Range)	57 (25 – 103)	Average (Range)		123 (66 – 158)		

Table 4-2 Summary of 24-hour and 1-hour TSP Monitoring Results at AC04c

Date	24-hour TSP ($\mu\text{g}/\text{m}^3$)	1-hour TSP ($\mu\text{g}/\text{m}^3$)				
		Date	Start Time	1 st hour measured	2 nd hour measured	3 rd hour measured
2-May-13	30	30-Apr-13	8:00	129	137	136
8-May-13	13	6-May-13	9:05	139	147	142
14-May-13	12	10-May-13	8:00	114	128	133
20-May-13	14	16-May-13	13:00	131	139	125
25-May-13	14	22-May-13	12:55	62	68	63
Average (Range)	15 (12 – 13)	Average (Range)		120 (62 – 147)		

4.03 As shown in *Tables 4-1 and 4-2*, the 1-hour and 24-hour TSP monitoring results fluctuated below the Action Level during this Reporting Period. No Notification of Exceedance (NOE) of air quality criteria or corrective action was therefore required.

4.04 The meteorological information during the impact monitoring days are summarized in *Appendix I*.

5 IMPACT MONITORING RESULTS – CONSTRUCTION NOISE

5.01 The noise monitoring results are presented in the following sub-sections.

Result

5.02 In this report period, 5 construction noise monitoring events were undertaken at designated location NC05. The results for $L_{eq(30min)}$ are tabulated in *Tables 5-1* and the graphical plots are shown in *Appendix H*.

Table 5-1 Summarized of Construction Noise Monitoring Results at NC05

Date	Start Time	End Time	1 st set L_{eq5}	2 nd set L_{eq5}	3 rd set L_{eq5}	4 th set L_{eq5}	5 th set L_{eq5}	6 th set L_{eq5}	L_{eq30}	Corrected L_{eq30}^*
30-Apr-13	9:47	10:17	66.1	63.1	66.0	65.6	61.1	53.9	64.1	67.1
6-May-13	9:22	9:52	62.4	60.2	60.1	60.3	60.0	60.3	60.6	63.6
10-May-13	9:43	10:13	61.2	61.1	61.7	62.8	63.2	62.1	62.1	65.1
16-May-13	11:12	11:42	53.6	56.9	57.6	57.1	58.0	59.2	57.4	60.4
22-May-13	10:43	11:13	61.2	61.0	59.7	58.1	57.3	58.9	59.6	62.6
Limit Level									-	75 dB(A)

* A façade correction of +3dB(A) has been added according to acoustical principles and EPD guidelines.

5.03 It was noted that no noise complaint (which is an Action Level exceedance) was received. In view of the results shown in *Table 5-1*, all the values are well below 75dB(A), therefore, no Action or Limit Level exceedance was triggered during this Reporting Period.

6 IMPACT MONITORING RESULTS – WATER QUALITY

- 6.01 In this Reporting Period, **12** days of water quality monitoring were carried out at the designated locations.
- 6.02 Field measurements of both control and impact stations showed that marine water of the depth average of the salinity concentration was within **29.07 to 36.66** ppt, and pH value was within **7.00 to 8.88**. The monitoring results including in-situ measurements and laboratory testing results are presented in [Appendix G](#). The graphical plots are shown in [Appendix H](#).
- 6.03 Monitoring results of 3 key parameters: dissolved oxygen (DO), turbidity and suspended solids in this Reporting Period, are summarized in [Tables 6-1, 6-2, 6-3 and 6-4](#). A summary of exceedances for the three parameters: dissolved oxygen (DO), turbidity and suspended solids are shown in [Table 6-5](#).

Table 6-1 Summary of Water Quality Results – Mid-ebb Tides (Dissolved Oxygen)

Sampling date	Dissolved Oxygen conc. of Depth Ave. of Surf. and Mid Layer (mg/L)					Dissolved Oxygen conc. of Depth Ave. of Bottom Layer (mg/L)				
	WY1	WY2	WY3	CY1	CY2	WY1	WY2	WY3	CY1	CY2
26-Apr-13	8.73	7.00	7.68	7.61	7.30	8.35	7.18	7.57	7.51	7.03
30-Apr-13	6.60	6.20	6.49	6.61	8.23	6.45	6.39	6.48	6.11	8.18
2-May-13	7.28	7.70	7.63	8.16	7.35	7.72	8.25	8.10	8.36	7.41
4-May-13	7.09	7.34	7.28	7.26	7.14	7.05	6.57	7.28	7.04	6.91
6-May-13	6.97	7.05	6.87	6.77	6.59	6.99	6.72	6.86	6.66	7.26
8-May-13	7.56	7.83	8.01	7.92	7.85	7.87	7.70	7.76	7.87	8.13
10-May-13	10.09	8.62	8.47	8.60	8.40	8.76	8.29	8.44	8.54	8.47
14-May-13	8.37	7.92	7.46	7.90	8.54	7.97	8.06	7.61	8.02	8.18
16-May-13	7.40	8.38	8.09	8.36	7.77	7.27	8.13	7.51	8.08	7.82
18-May-13	7.73	8.07	7.67	8.32	7.70	8.08	8.36	8.33	8.33	7.60
20-May-13	9.06	8.33	8.58	7.83	8.47	7.29	7.43	7.31	7.42	8.69
24-May-13	7.46	7.69	7.20	7.28	7.37	7.71	7.68	7.81	7.44	7.37

Table 6-2 Summary of Water Quality Results – Mid-ebb Tides (Turbidity & Suspended Solids)

Sampling date	Turbidity Depth Ave. (NTU)					Suspended Solids Depth Ave. (mg/L)				
	WY1	WY2	WY3	CY1	CY2	WY1	WY2	WY3	CY1	CY2
26-Apr-13	2.27	1.88	2.41	1.75	1.66	2.90	5.87	3.50	6.80	3.17
30-Apr-13	1.13	1.43	1.22	1.22	1.33	5.05	3.83	3.75	2.53	3.00
2-May-13	2.26	2.00	2.22	1.86	1.78	5.45	4.83	5.25	9.07	5.00
4-May-13	2.21	1.62	1.97	1.57	1.75	8.05	7.27	3.15	3.57	4.43
6-May-13	2.86	2.24	2.76	1.96	2.12	3.45	5.60	5.30	8.23	4.23
8-May-13	2.28	2.11	2.03	1.65	1.75	7.10	7.07	8.80	5.80	8.67
10-May-13	3.76	2.37	3.72	2.13	2.16	5.00	4.50	7.20	2.53	5.27
14-May-13	1.53	1.52	1.58	1.36	1.30	3.65	1.57	5.25	1.73	2.57
16-May-13	2.65	1.95	2.50	1.79	1.62	5.40	6.33	6.30	5.40	8.23
18-May-13	5.39	2.77	3.13	2.25	2.12	2.50	5.40	4.00	4.47	4.43
20-May-13	3.06	2.83	3.14	2.69	2.63	6.95	5.60	6.55	4.67	5.93
24-May-13	3.63	3.03	3.51	2.84	2.99	2.70	4.03	4.25	3.03	2.07

Table 6-3 Summary of Water Quality Results – Mid-flood Tides (Dissolved Oxygen)

Sampling date	Dissolved Oxygen conc. of Depth Ave. of Surf. and Mid Layer (mg/L)					Dissolved Oxygen conc. of Depth Ave. of Bottom Layer (mg/L)				
	WY1	WY2	WY3	CY1	CY2	WY1	WY2	WY3	CY1	CY2
26-Apr-13	6.76	7.26	7.19	7.82	8.25	6.58	7.36	6.86	7.66	8.27
30-Apr-13	6.95	6.92	6.38	6.76	7.23	6.51	6.82	5.64	6.28	5.94
2-May-13	7.49	7.53	7.37	7.36	6.60	6.82	7.37	7.03	7.36	6.87
4-May-13	7.32	7.34	7.32	7.35	7.02	7.31	7.17	7.35	7.11	6.82
6-May-13	6.97	6.94	6.51	7.06	6.58	6.52	6.86	6.09	6.79	6.31

8-May-13	8.55	8.58	8.55	8.91	8.42	8.36	8.63	8.74	8.87	8.05
10-May-13	6.46	5.88	6.30	6.35	8.16	6.24	5.91	6.37	5.28	7.83
14-May-13	8.10	7.81	7.54	7.38	7.49	7.55	7.58	7.35	7.31	6.80
16-May-13	7.98	8.03	8.15	8.16	8.27	8.16	8.22	7.93	8.42	8.11
18-May-13	7.83	8.82	7.67	8.77	8.06	8.17	8.68	7.78	8.55	7.31
20-May-13	9.10	8.57	9.33	8.39	8.27	7.44	7.40	7.38	7.19	7.07
24-May-13	7.38	7.36	7.17	7.09	6.50	7.40	7.25	7.40	6.96	6.39

Table 6-4 Summary of Water Quality Results – Mid-flood Tides (Turbidity & Suspended Solids)

Sampling date	Turbidity Depth Ave. (NTU)					Suspended Solids Depth Ave. (mg/L)				
	WY1	WY2	WY3	CY1	CY2	WY1	WY2	WY3	CY1	CY2
26-Apr-13	1.73	1.45	1.82	1.32	1.52	9.70	3.30	2.85	3.30	5.30
30-Apr-13	1.49	1.21	1.42	1.02	1.04	7.35	6.27	6.75	4.20	4.43
2-May-13	1.91	1.74	1.94	1.68	1.60	5.60	4.77	5.95	5.37	5.87
4-May-13	1.66	1.46	1.76	1.26	1.25	6.55	5.50	5.40	3.80	4.60
6-May-13	2.02	1.66	2.12	1.37	1.47	11.95	7.70	10.45	10.40	8.60
8-May-13	1.77	1.77	1.68	1.51	1.38	9.00	13.07	8.75	11.30	10.83
10-May-13	2.36	1.98	2.49	1.85	1.96	4.35	4.00	4.35	3.07	6.47
14-May-13	1.32	1.24	1.28	1.11	1.07	2.70	2.07	2.60	3.77	2.33
16-May-13	2.17	1.84	2.06	1.67	1.50	8.35	9.03	5.85	6.53	7.40
18-May-13	2.35	2.05	2.28	1.85	31.31	3.85	4.00	4.05	4.57	1.83
20-May-13	2.61	2.44	2.63	2.19	2.12	5.90	6.17	4.65	7.17	6.50
24-May-13	2.50	2.21	2.54	2.02	1.88	7.55	5.50	8.95	2.80	6.87

Table 6-5 Summarized Exceedances of Marine Water Quality

Station	DO (Ave of Surf. & mid-depth)		DO (Ave. of Bottom Layer)		Turbidity (Depth Ave.)		SS (Depth Ave)		Total Exceedance	
	Action	Limit	Action	Limit	Action	Limit	Action	Limit	Action	Limit
Mid-Ebb										
WY1	0	0	0	0	0	0	0	0	0	0
WY2	0	0	0	0	0	0	0	0	0	0
WY3	0	0	0	0	0	0	0	0	0	0
Mid-Flood										
WY1	0	0	0	0	0	0	0	0	0	0
WY2	0	0	0	0	0	0	0	0	0	0
WY3	0	0	0	0	0	0	0	0	0	0
No of Exceedance	0	0	0	0	0	0	0	0	0	0

6.04 For marine water monitoring, no exceedance of Action/Limit level was recorded in this Reporting Period. Therefore, no associated corrective actions were then required.

7 IMPACT MONITORING RESULTS – ECOLOGY MONITORING

- 7.01 Impact monitoring for coral shall be conducted initially at a frequency of once per week for the first three months of the marine works (HDD and dredging). If no exceedances are reported during this period, then the frequency may be reduced to twice every month for the remainder of the marine works.
- 7.02 According to the construction information provided by the Contractor, the marine works in Yung Shue Wan has been completed on 22 April 2013. In this Reporting Period, as agreed by the Contractor, the ecology monitoring was ceased due to no ecological impact and concern since the completion of marine work.

8 WASTE MANAGEMENT

8.01 Waste management was carried out by an on-site Environmental Officer or an Environmental Supervisor from time to time.

Records of Waste Quantities

8.02 All types of waste arising from the construction work are classified into the following:

- Construction & Demolition (C&D) material;
- Chemical waste;
- General refuse; and
- Excavated soil.

8.03 The quantities of waste for disposal in this Reporting Period are summarized in [Tables 8-1](#) and [8-2](#) and the Monthly Summary Waste Flow Table is shown in [Appendix J](#). Whenever possible, materials were reused on-site as far as practicable.

Table 8-1 Summary of Quantities of Inert C&D Materials

Type of Waste	Quantity	Disposal Location
C&D Materials (Inert) ('000m ³)	0	-
Reused in this Contract (Inert) ('000m ³)	0	-
Reused in other Projects (Inert) ('000m ³)	0	-
Disposal as Public Fill (Inert) ('000m ³)	0	Tuen Mun Area 38

Table 8-2 Summary of Quantities of C&D Wastes

Type of Waste	Quantity	Disposal Location
Metals (kg)	0	-
Paper / Cardboard Packing (kg)	0	-
Plastics (kg)	0	-
Chemical Wastes (kg)	0	-
General Refuses (tonne)	1.790	Yung Shue Wan RTS

8.04 There was no site effluent discharged but the estimated volume of surface runoff was less than 50m³ in this monthly period.

9 SITE INSPECTION

- 9.01 According to the Environmental Monitoring and Audit Manual, the environmental site inspection should be formulated by ET Leader. Regular environmental site inspections had been carried out by the ET to confirm the environmental performance. In this Reporting Period, weekly joint-site visit by RE, the Contractor and ET was carried out on **30 April, 7, 14 and 21 May 2013**.
- 9.02 The findings/ deficiencies that observed during the weekly site inspection are listed in *Table 9-1* and the relevant checklists are attached in *Appendix K*.

Table 9-1 Site Observations

Date	Findings / Deficiencies	Follow-Up Status
30 April 2013	<ul style="list-style-type: none"> Stagnant water was observed on the roof floor, posing potential of mosquito breeding. Clearance of the stagnant water is required. 	Stagnant water was dried off and mosquito control measures were observed on 7 May 2013.
7 May 2013	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection. However, full implementation of the required clearance of the stagnant water due to rain is reminded. 	N.A.
14 May 2013	<ul style="list-style-type: none"> No environmental issue was observed during the site inspection. However, full implementation of the required clearance of the stagnant water due to rain is reminded. 	N.A.
21 May 2013	<ul style="list-style-type: none"> HVS was covered by climbing plant. Removal of the plant is required. Stagnant water due to heavy rain was observed within the site (on the roof of the Sewage Treatment Plant). Regular clearance is required to avoid mosquito breeding. Direct discharge of rainwater from roof was observed. Pretreatment of the rainwater prior to discharge is required. 	<ul style="list-style-type: none"> Climbing plant around HVS was cleared on 28 May 2013. Mosquito control measures were observed on 28 May 2013. Direct discharge was not observed. Sedimentation tank was used.

10 ENVIRONMENTAL COMPLAINT AND NON-COMPLIANCE

10.01 No environmental complaint, summons and prosecution was received in this reporting period. The statistical summary table of environmental complaint is presented in *Tables 10-1, 10-2* and *10-3*.

Table 10-1 Statistical Summary of Environmental Complaints

Reporting Period	Environmental Complaint Statistics		
	Frequency	Cumulative	Complaint Nature
14 Sep – 30 September 2011	0	0	NA
October – December 2011	0	0	NA
January –December 2012	0	0	NA
January - April 2013	0	0	NA
May 2013	0	0	NA

Table 10-2 Statistical Summary of Environmental Summons

Reporting Period	Environmental Summons Statistics		
	Frequency	Cumulative	Complaint Nature
14 Sep – 30 September 2011	0	0	NA
October – December 2011	0	0	NA
January –December 2012	0	0	NA
January - April 2013	0	0	NA
May 2013	0	0	NA

Table 10-3 Statistical Summary of Environmental Prosecution

Reporting Period	Environmental Prosecution Statistics		
	Frequency	Cumulative	Complaint Nature
14 Sep – 30 September 2011	0	0	NA
October – December 2011	0	0	NA
January –December 2012	0	0	NA
January - April 2013	0	0	NA
May 2013	0	0	NA

11 IMPLEMENTATION STATUS OF MITIGATION MEASURES

11.01 The environmental mitigation measures that recommended in the Yung Shue Wan Environmental Monitoring and Audit Manual covered the issues of dust, noise, water and waste and they are summarized as following:

Dust Mitigation Measure

11.02 Installation of 2m high solid fences around the construction site of Pumping Station P2 is recommended. Implementation of the requirements stipulated in the Air Pollution Control (Construction Dust) Regulation and the following good site practices are recommended to control dust emission from the site:

- Stockpiles of imported material kept on site should be contained within hoardings, dampened and / or covered during dry and windy weather;
- Material stockpiled alongside trenches should be covered with tarpaulins whenever works are close to village houses;
- Water sprays should be used during the delivery and handling of cement, sands, aggregates and the like.
- Any vehicle used for moving sands, aggregates and construction waste shall have properly fitting side and tail boards. Materials should not be loaded to a level higher than the side and tail boards, and should be covered by a clean tarpaulin.

Noise Mitigation Measure

11.03 As detailed in the EIA report, concreting work of the Pumping Station P1a and sewer alignment construction activities would likely cause adverse noise impacts on some of the noise sensitive receivers. Appropriate mitigation measures have therefore been recommended. The mitigation measures recommended in the EIA report are summarised below:

- (a) Use of quiet equipment for the construction activities of the Pumping Stations and sewer alignment;
- (b) Use of temporary noise barrier around the site boundary of Pumping Station P1a;
- (c) Use of kick ripper (saw and lift) method to replace the breaker for pavement removal during sewer alignment construction;
- (d) Restriction on the number of plant during sewer alignment construction;
- (e) Use of noise screening structures in the form of acoustic shed or movable barrier wherever practicable and feasible in areas with sufficient clearance and headroom during the construction of sewer alignment;
- (f) Adoption of manual working method wherever practicable and feasible in areas where the worksites of the proposed sewer alignment are located less than 20m from the residential noise sensitive receivers and less than 30m from the temple and the public library; and
- (g) Implementation of the following good site practices:
 - Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme.
 - Mobile plant, if any, should be sited as far away from NSRs as possible.
 - Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum.
 - Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs.
 - Material stockpiles and other structures should be effectively utilised, wherever practicable, in screening noise from on-site construction activities.

Water Quality Mitigation Measure

11.04 No-dig method using Horizontal Directional Drilling (HDD) would be used for the installation of outfall pipe of about 480 m from shore to minimize the potential water quality impacts arising from the dredging works required for the submarine outfall construction. For the remaining outfall pipe of about 240m and the diffuser section, open trench dredging would still be required.

- 11.05 During the dredging works, the Contractor should be responsible for the design and implementation of the following mitigation measures.
- Dredging should be undertaken using closed grab dredgers with a total production rate of 55m³/hr;
 - Deployment of 2-layer silt curtains with first layer enclosing the grab and the second layer at around 50, from the dredging area while dredging works are in progress;
 - all vessels should be sized such that adequate clearance (i.e. minimum clearance of 0.6m) is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash;
 - all pipe leakages should be repaired promptly and plant shall not be operated with leaking pipes;
 - excess material should be cleaned from the decks and exposed fittings of barges before the vessel is moved;
 - adequate freeboard (i.e. minimum of 200m) should be maintained on barges to ensure that decks are not washed by wave action;
 - all barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material;
 - loading of barges and hoppers should be controlled to prevent splashing of dredged material to the surrounding water, and barges and hoppers should not be filled to a level which would cause the overflow of materials or sediment laden water during loading or transportation; and
 - the decks of all vessels should be kept tidy and free of oil or other substances that might be accidentally or otherwise washed overboard.

Construction Run-off and Drainage

- 11.06 The Contractor should observe and comply with the Water Pollution Control Ordinance and the subsidiary regulations. The Contractor should follow the practices, and be responsible for the design, construction, operation and maintenance of all the mitigation measures as specified in ProPECC PN 1/94 “Construction Site Drainage”. The design of the mitigation measures should be submitted by the Contractor to the Engineer for approval. These mitigation measures should include the following practices to minimise site surface runoff and the chance of erosion, and also to retain and reduce any suspended solids prior to discharge:
- Provision of perimeter channels to intercept storm-runoff from outside the site. These should be constructed in advance of site formation works and earthworks.
 - Works programmes should be designed to minimize works areas at any one time, thus minimising exposed soil areas and reducing the potential for increased siltation and runoff.
 - Sand/silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove the sand/silt particles from run-off. These facilities should be properly and regularly maintained. These facilities shall be carefully planned to ensure that they would be installed at appropriate locations to capture all surface water generated on site.
 - Careful programming of the works to minimise soil excavation works during rainy seasons.
 - Exposed soil surface should be protected by paving or hydroseeding as soon as possible to reduce the potential of soil erosion.
 - Trench excavation should be avoided in the wet season, and if necessary, these should be excavated and backfilled in short sections.
 - Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric.

General Construction Activities

- 11.07 Debris and rubbish generated on-site should be collected, handled and disposed of properly to avoid entering the nearby coastal waters and stormwater drains. All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Open drainage channels and culverts near the works areas should be covered to block the entrance of large debris and refuse.

Wastewater Arising from Workforce

- 11.08 Portable toilets shall be provided by the Contractors, where necessary, to handle sewage from the workforce. The Contractor shall also be responsible for waste disposal and maintenance practices

Sediment Contamination Mitigation Measure

- 11.09 The basic requirements and procedures for dredged mud disposal are specified under the WBTC No. 34/2002. The management of the dredging, use and disposal of marine mud is monitored by the MFC, while the licensing of marine dumping is the responsibility of the Director of Environmental Protection (DEP).
- 11.10 The uncontaminated dredged sediment will be loaded onto barges and transported to the designated marine disposal site. Appropriate dredging methods have been incorporated into the recommended water quality mitigation measures including the use of closed-grab dredgers and silt curtains. Category L sediment would be suitable for disposal at a gazetted open sea disposal ground.
- 11.11 During transportation and disposal of the dredged marine sediments, the following measures should be taken to minimize potential impacts on water quality:
- Bottom opening of barges should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved.
 - Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self-monitoring devices as specified by the DEP.

Construction Waste Mitigation Measure

Good Site Practices and Waste Reduction Measures

- 11.12 It is not anticipated that adverse waste management related impacts would arise, provided that good site practices are strictly followed. Recommendations for good site practices for the construction waste arising include:
- Nomination of an approved person, such as a site manager, to be responsible for the implementation of good site practices, arranging for collection and effective disposal to an appropriate facility, of all wastes generated at the site.
 - Training of site personnel in proper waste management and chemical handling procedures.
 - Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers.
 - Provision of sufficient waste disposal points and regular collection for disposal.
 - Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility.
 - Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors.
 - Maintain records of the quantities of wastes generated, recycled and disposed.
- 11.13 In order to monitor the disposal of C&D waste at landfills and to control fly tipping, a trip-ticket system should be included as one of the contractual requirements and implemented by an Environmental Team undertaking the Environmental Monitoring and Audit work. An Independent Environmental Checker should be responsible for auditing the results of the system.
- 11.14 Good management and control can prevent the generation of significant amount of waste. Waste reduction is best achieved at the planning and design stage, as well as by ensuring the implementation of good site practices. Recommendations to achieve waste reduction include:
- segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal;

- to encourage collection of aluminium cans by individual collectors, separate labelled bins should be provided to segregate this waste from other general refuse generated by the work force;
- any unused chemicals or those with remaining functional capacity should be recycled;
- use of reusable non-timber formwork to reduce the amount of C&D material;
- prior to disposal of C&D waste, it is recommended that wood, steel and other metals should be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill;
- proper storage and site practices to minimise the potential for damage or contamination of construction materials; and
- plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste.

General Site Wastes

- 11.15 A collection area should be provided where waste can be stored prior to removal from site. An enclosed and covered area is preferred for the collection of the waste to reduce 'wind blow' of light material.

Chemical Wastes

- 11.16 After use, chemical waste (eg. cleaning fluids, solvents, lubrication oil and fuel) should be handled according to the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. Any unused chemicals or those with remaining functional capacity should be recycled. Spent chemicals should be properly stored on site within suitably designed containers, and should be collected by an approved operator for disposal at the Chemical Waste Treatment Facility or other licenced facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation under the Waste Disposal Ordinance.
- 11.17 Any service shop and minor maintenance facilities should be located on hard standings within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakages and spillage should only be undertaken with the areas appropriately equipped to control these discharges.

Construction and Demolition Material

- 11.18 The C&D material should be separated on-site into three categories: (i) public fill, the inert portion of the C&D material (e.g. concrete and rubble), which should be re-used on-site or disposed of at a public filling area; (ii) C&D waste for re-use and/or recycling, the non-inert portion of the C&D material, (e.g. steel and other metals, wood, glass and plastic); (iii) C&D waste which cannot be re-used and/or recycled. The waste producers are responsible for its disposal at strategic landfills.
- 11.19 In order to minimise the impact resulting from collection and transportation of material for off-site disposal, it was recommended that inert material should be re-used on-site where possible. Prior to disposal of C&D material, it was also recommended that steel and other metals should be separated for re-use and/or recycling where practicable to minimise the quantity of waste to be disposed of to landfill.

Ecology Mitigation Measure

- 11.20 The following general good practice measures should be adopted to mitigate ecological impacts during marine works (including dredging and HOD);
- Excess material from vessel loading should be cleaned from the decks and exposed fittings before vessels are moved to the backfilling location;
 - Dredging should cause no foam, oil, grease, scum, litter or other objectionable matter to be present on the water;
 - Adequate freeboard should be maintained to ensure that decks are not washed by wave action;

- All pie leakages should be repaired promptly and plant Should not be operated with leaking pipes; and
 - All banges and other vessels should maintain adequate clearance between vessels and the seabed at all stats of the tide and reduce operational speeds to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash.
- 11.21 In the event of exceedances of ecological action or limit level, the Contractor will be required to revise his operations as a further mitigation measure. Revisions to the operation method may include (but not be limited to):
- Reduction in dredging rate'
 - Restriction of dredging in particular areas to specific periods in the tidal cycle
- 11.22 Should repeated non-compliances with limit level(s) occur the Contractor shall modify his working method until he is able to achieve the required compliances with the limit levels to the satisfaction of the IC(E)

Fisheries Mitigation Measure

- 11.23 Closed grab dredger, deployment of silt curtains around the immediate dredging area and low dredging rate have been recommended in Water Quality of the EIA report in order to minimise sediment release into the water column.

Landscape & Visual Mitigation Measure

- 11.24 Mitigation measures recommended in the EIA Report for landscape and visual impacts during the construction stage are summarised below.
- Screening of site construction works by use of hoarding that is appropriate to its site context;
 - Retaining existing trees and minimising damage to vegetation where possible by close co-ordination and on site alignment adjusted of rising main and gravity sewer pipelines. Tree protective measures should be implemented to ensure trees identified as to be retained are satisfactorily protected during the construction phase;
 - Careful and efficient transplanting of affected trees (1 no.) to temporary or final transplant location (the proposed tree to be transported is a semi-mature *Macaranga tanarius* and is located at the proposed Pumping Station P2 location);
 - Short excavation and immediate backfilling of sections upon completion of works to reduce active site area;
 - Conservation of top-soil for reuse;
 - Night-time light source from marine fleets should be directed away from the residential units
- 11.25 The implementation schedule of mitigation measures is presented in [Appendix L](#).
- 11.26 Leader had been implementing the required environmental mitigation measures according to the Yung Shue Wan Environmental Monitoring and Audit Manual subject to the site condition. Environmental mitigation measures generally implemented by Leader in this Reporting Period are summarized in [Table 11-1](#).

Table 11-1 Environmental Mitigation Measures

Issues	Environmental Mitigation Measures
Water Quality	<ul style="list-style-type: none"> • Drainage channels were provided to convey run-off into the treatment facilities; and • Drainage systems were regularly and adequately maintained.

Issues	Environmental Mitigation Measures
Air Quality	<ul style="list-style-type: none"> • Cover all excavated or stockpile of dusty material by impervious sheeting or sprayed with water to maintain the entire surface wet; • Public roads around the site entrance/exit had been kept clean and free from dust; and • Tarpaulin covering of any dusty materials on a vehicle leaving the site.
Noise	<ul style="list-style-type: none"> • Good site practices to limit noise emissions at the sources; • Use of quiet plant and working methods; • Use of site hoarding or other mass materials as noise barrier to screen noise at ground level of NSRs; and • To minimize plant number use at the worksite.
Waste and Chemical Management	<ul style="list-style-type: none"> • Excavated material should be reused on site as far as possible to minimize off-site disposal. Scrap metals or abandoned equipment should be recycled if possible; • Waste arising should be kept to a minimum and be handled, transported and disposed of in a suitable manner; • The Contractor should adopt a trip ticket system for the disposal of C&D materials to any designed public filling facility and/or landfill; and • Chemical waste shall be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of Chemical Wastes.
General	<ul style="list-style-type: none"> • The site was generally kept tidy and clean.

12 IMPACT FORECAST

12.01 Key issues to be considered in the coming month include:

Water Quality

- Erect of sand bag in proper area to avoid any muddy surface runoff from the loose soil surface or haul road during the rainy days; and
- The accumulated stagnant water should be drained away.

Air Quality

- Vehicles shall be cleaned of mud and debris before leaving the site;
- Stockpile and loose soil surface shall be covered with tarpaulin sheet or other means to eliminate the fugitive dust;
- Water spaying on the dry haul road and exit/entrance of the site in regular basis is reminded; and
- Public roads around the site entrance/exit had been kept clean and free from dust.

Noise

- Works and equipment should be located to minimize noise nuisance from the nearest sensitive receiver; and
- Idle equipments should be either turned off or throttled down;

Waste and Chemical Management

- Housekeeping on site shall be improved;
- The Contractor is advised to fence off the construction waste at a designated area in order to maintain the tidiness of the site;
- Drip tray and proper label should be provided for all chemical containers.
- C&D waste should be disposed in regular basis.

13 CONCLUSIONS AND RECOMMENDATIONS

CONCLUSIONS

- 13.01 This is the 33rd Monthly EM&A Report covering the construction period from 26 April to 25 May 2013.
- 13.02 No 1-hour and 24-hour TSP result was found to be triggered the Action or Limit Level in this Reporting Period.
- 13.03 No noise complaint (an Action Level exceedance) was received and no construction noise measurement results that exceeded the Limit Level were recorded in this Reporting Period.
- 13.04 No marine water monitoring exceedance was recorded in this Reporting Period.
- 13.05 According to the construction information provided by the Contractor, the marine works in Yung Shue Wan has been completed on 22 April 2013. In this Reporting Period, as agreed by the Contractor, the ecology monitoring was ceased due to no ecological impact and concern since the completion of marine work.
- 13.06 No documented complaint, notification of summons or successful prosecution was received.
- 13.07 In this Reporting Period, joint-site visit by RE, the Contractor and ET was carried out on 30 April, 7, 14 and 21 May 2013. The environmental performance of the Project was considered as satisfactory.
- 13.08 No site inspection was undertaken by external parties i.e. Environmental Protection Department (EPD) or Agriculture, Fisheries and Conservation Department (AFCD) within the Reporting Period.

RECOMMENDATIONS

- 13.09 During wet season, the Contractor shall pay attention on the potential water impact as the construction site is adjacent to the coastline. Muddy water and other water quality pollutants via site surface water runoff into the coral zones of Yung Shue Wan seawall, Shek Kok Tsui and O Tsai should be avoided. Mitigation measures for water quality should be fully implemented.
- 13.10 Nevertheless, the Contractor shall keep paying attention on the potential water impact as the construction site is adjacent to the coastline. Muddy water and other water quality pollutants via site surface water runoff into the sea body within Fish culture zone at Picnic Bay and the Secondary recreation contact subzone at Mo Tat Wan should be avoided. Therefore, mitigation measures for water quality should be fully implemented.

Appendix A

Site Layout Plan – Yung Shue Wan Portion Area

Appendix B

Organization Structure and Contact Details of Relevant Parties

Contact Details of Key Personnel

Organization	Project Role	Name of Key Staff	Tel No.	Fax No.
DSD	Employer	Ms. Jacky C.M. Wong	2159-3413	2833-9162
SCJV	Engineer's Representative	Mr. Ian Jones	2982 0240	2982 4129
SCJV	Resident Engineer	Mr. Alfred Cheung	2982 0240	2982 4129
URS	Independent Environmental Checker	Mr. Rodney Ip	2410 3750	2428 9922
Leader	Director	Mr. Wilfred So	2982 1750	2982 1163
Leader	Project Manager	Mr. Vincent Chan	2982 1750	2982 1163
Leader	Construction Manager	Mr. K. Y. So	2982 1750	2982 1163
Leader	Site Agent	Mr. Ron Hung	2982 1750	2982 1163
Leader	Environmental Officer	Mr. K. Y. So	2982 8652	2982 8650
Leader	Environmental Supervisor	Mr. Chan Shut Man	2982 8652	2982 8650
Leader	Sub-Agent	Mr. Burgess Yip	2982 1750	2982 1163
Leader	Senior Safety Officer	Mr. Edwin Leung	2982 1750	2982 1163
AUES	Environmental Team Leader	Mr. T. W. Tam	2959 6059	2959 6079
AUES	Environmental Consultant	Ms. Nicola Hon	2959 6059	2959 6079
AUES	Team Supervisor	Mr. Ben Tam	2959 6059	2959 6079
AUES	Coral Specialist	Mr. Keith Kei	2959 6059	2959 6079

Legend:

DSD (Employer) – Drainage Services Department

CDM (Engineer) – Scott Wilson CDM Joint Venture

Leader (Main Contractor) – Leader Civil Engineering Corporation Limited

URS (IEC) – URS Hong Kong Limited

AUES (ET) – Action-United Environmental Services & Consulting

Appendix C

Master and Three Months Rolling Construction Programme

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013			
											APR	MAY	JUN	JUL
Project Key Date														
KD0010	Receive Letter of Acceptance	0	100		05/05/10 A		05/05/10 A			KD0125				
KD0020	Project Commencement Date	0	100		17/05/10 A		17/05/10 A			E&M0010, E&M0070, E&M1001, E&M2001, KD0125, PRE0020, PRE0040, PRE0050, PRE0060, PRE0090, PRE0100, PRE0130, SKW0250, SKW0588, SKW0651, SKW0681, SKW1131, SKW1481, SKW1591, SKW1611, YSW0020, YSW0050, YSW0075, YSW0180, YSW0200, YSW0220, YSW0240, YSW02401, YSW0412, YSW0422				
KD0030	Section W1 - Slope Works in Portion A & C	0	100		14/10/11 A		14/10/11 A		YSW0100, YSW0110, YSW0140,	KD0125, KD0130, YSW01755				
KD0040	Section W2 - YSW STW & Submarine Outfall (1370d)	0	0		16/06/14 *		16/06/14 *	0 *	E&M0700, YSW0400, YSW0800, YSW0870, YSW0925, YSW16704, YSW1700	KD0125, KD0132				
KD0050	Section W3 - Footpath Diversion in Ptn G	0	0		29/04/13 *		24/03/11 *	-767d *	SKW0481	KD0125				
KD0060	Section W4 - Slope Works in Portios H & I	0	0		29/04/13 *		27/03/12 *	-398d *	SKW05938, SKW059416	KD0125, KD0135, SKW05941				
KD0070	Section W5 - P.S. No. 1 in Portion D	0	0		29/04/13 *		10/02/12 *	-444d *	SKW0741	KD0125				
KD0080	Section W6 - Sewer & PS No2 in Ptn. E & F	0	0		29/04/13 *		10/02/12 *	-444d *	SKW0971	KD0125				
KD0090	Section W7 - SKW STW, RM & Sm. Outfall	0	0		07/10/14 *		07/10/14 *	0 *	E&M3360, SKW1221, SKW1291, SKW1431, SKW1441, SKW1521,	KD0125, KD0165, SKW0491				
KD0100	Section W8 - Landscape Softworks	0	0		29/04/13 *		05/04/13 *	-24d *	SKW1611, SKW1621					
KD0110	Section W9 - Establishment Works	0	0		03/04/14 *		03/04/14 *	0 *	SKW1631	KD0125				
KD0125	Project Completion	0	0		12/09/15 *		12/09/15 *	0 *	KD0010, KD0020, KD0030, KD0040, KD0050, KD0060, KD0070, KD0080, KD0090, KD0110, SKW0541					
KD0130	Completion of Maintenance Period of W1	1	0	30/04/13	30/04/13 *	13/10/12	13/10/12 *	-199d	KD0030, YSW01755, YSW01805, YSW01810					
KD0132	Completion of Maintenance Period of W2	1	0	15/06/15	15/06/15 *	15/06/15	15/06/15 *	0	E&M0730, KD0040					
KD0135	Completion of Maintenance Period of W4	1	0	30/04/13	30/04/13 *	27/03/13	27/03/13 *	-34d	KD0060, SKW05947, SKW1581					
KD0145	Completion of Maintenance Period of W5	1	0	30/04/13	30/04/13 *	10/02/13	10/02/13 *	-79d						
KD0155	Completion of Maintenance Period of W6	1	0	30/04/13	30/04/13 *	10/02/13	10/02/13 *	-79d	E&M2130, E&M2180, SKW0961,					
KD0165	Completion of Maintenance period of W7	1	0	06/10/15	06/10/15 *	06/10/15	06/10/15 *	0 *	KD0090, SKW0595, SKW05972, SKW0861					
Preliminary (Civil)														
PRE0020	Pre-condition Survey	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A		KD0020					
PRE0040	Erection of Engineer's Site Accommodation at YSW	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A		KD0020					
PRE0050	Taking over the Secondary Engineer's Site Accom	75	100	17/05/10 A	30/07/10 A	17/05/10 A	30/07/10 A		KD0020					
PRE0060	Application of Consent from Marine Department	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A		KD0020					
PRE0090	Working Group Meeting for Outfall Construction	120	100	17/05/10 A	13/09/10 A	17/05/10 A	13/09/10 A		KD0020	SKW1151				
PRE0100	Application & Consent of XP from HyD (Mo Tat Rd)	120	100	17/05/10 A	13/09/10 A	17/05/10 A	13/09/10 A		KD0020	SKW1491, SKW1501				
PRE0130	Setup Web-site for EM&A Reporting	90	100	17/05/10 A	14/08/10 A	17/05/10 A	14/08/10 A		KD0020					
Preliminary (E&M)														
Technical Submission														
Process Design of SKWSTW & YSWSTW														
E&M0010	Submission	38	100	17/05/10 A	23/06/10 A	17/05/10 A	23/06/10 A		KD0020	E&M0020, E&M0040, E&M0235				
E&M0020	Vetting and Comment by ER	21	100	24/06/10 A	14/07/10 A	24/06/10 A	14/07/10 A		E&M0010	E&M0030, E&M0040				
E&M0030	Revision and Resubmission	125	100	15/07/10 A	16/11/10 A	15/07/10 A	16/11/10 A		E&M0020	E&M0080				
E&M0080	Approval from the Engineer	14	100	17/11/10 A	30/11/10 A	17/11/10 A	30/11/10 A		E&M0030	E&M0295				
Hydraulic Design														
E&M0040	Submission	21	100	15/07/10 A	04/08/10 A	15/07/10 A	04/08/10 A		E&M0010, E&M0020	E&M0050, E&M0101, E&M0240, E&M0260,				
E&M0050	Vetting and Comment by ER	14	100	05/08/10 A	18/08/10 A	05/08/10 A	18/08/10 A		E&M0040	E&M0060				
E&M0060	Revision and Resubmission	97	100	19/08/10 A	10/10/10 A	19/08/10 A	10/10/10 A		E&M0050	E&M0430				
E&M0430	Approval from the Engineer	7	100	24/11/10 A	30/11/10 A	24/11/10 A	30/11/10 A		E&M0060	E&M0295				
Equipment Submission & Approval														
E&M0070	Submission of Membrane Module	50	100	17/05/10 A	05/07/10 A	17/05/10 A	05/07/10 A		KD0020	E&M0090				
E&M0090	Vetting and Comment by ER	14	100	06/07/10 A	19/07/10 A	06/07/10 A	19/07/10 A		E&M0070	E&M0100				
E&M0100	Revision and Resubmission	14	100	20/07/10 A	24/02/11 A	20/07/10 A	24/02/11 A		E&M0090	E&M0160				
E&M0101	Submission of Equipment	90	100	05/08/10 A	30/11/11 A	05/08/10 A	30/11/11 A		E&M0040	E&M0102				
E&M0102	Vetting and Comment by ER	60	100	03/11/10 A	30/11/11 A	03/11/10 A	30/11/11 A		E&M0101	E&M0103				

Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	1A
© Primavera Systems, Inc.	

	Early bar
	Progress bar
	Critical bar
	Summary bar
	Progress point
	Critical point
	Summary point
	Start milestone point
	Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013				
											APR	MAY	JUN	JUL	
E&M0103	Revision and Resubmission	60	100	01/02/11 A	30/11/11 A	01/02/11 A	30/11/11 A		E&M0102	E&M0110, E&M0120, E&M0130, E&M0140,					
E&M0110	Approval on Coarse Screens	30	100	25/05/11 A	25/05/11 A	25/05/11 A	25/05/11 A		E&M0103	E&M0390					
E&M0120	Approval on Fine Screens	30	100	12/09/11 A	12/09/11 A	12/09/11 A	12/09/11 A		E&M0103	E&M0400, E&M3060					
E&M0130	Approval on Pumps	30	100	23/06/11 A	23/06/11 A	23/06/11 A	23/06/11 A		E&M0103	E&M0410, E&M3070					
E&M0140	Approval on Submersible Mixers	30	100	23/03/11 A	23/03/11 A	23/03/11 A	23/03/11 A		E&M0103	E&M0420, E&M3080					
E&M0150	Approval on Grit Removal Equipment	30	100	10/10/11 A	10/10/11 A	10/10/11 A	10/10/11 A		E&M0103	E&M0380, E&M3030					
E&M0160	Approval on MBR Membrane Modules (MM)	105	100	03/08/10 A	24/02/11 A	03/08/10 A	24/02/11 A		E&M0100	E&M0360, E&M0370, E&M3010					
E&M0170	Approval on Sludge Dewatering Equipment	30	100	01/09/11 A	01/09/11 A	01/09/11 A	01/09/11 A		E&M0103	E&M0440, E&M3090					
E&M0180	Approval on Valves, Pipes & Fittings	30	85	19/11/11 A	04/05/13	19/11/11 A	15/04/13	-19d	E&M0103	E&M0450, E&M3100					
E&M0190	Approval on Penstocks	30	100	15/11/11 A	15/11/11 A	15/11/11 A	15/11/11 A		E&M0103	E&M0460, E&M3110					
E&M0200	Approval on Instrumentation	30	100	21/06/11 A	08/03/12 A	21/06/11 A	08/03/12 A		E&M0103	E&M0470, E&M3130					
E&M0210	Approval on MCC & LVSB	30	95	19/11/11 A	01/05/13	19/11/11 A	22/08/11	-618d	E&M0103	E&M0480, E&M3140					
E&M0220	Approval on BS Equipment	30	85	30/11/11 A	04/06/13	30/11/11 A	22/04/12	-408d	E&M0103, E&M0280	E&M0490, E&M3150					
E&M0230	Approval on FS Equipment	30	85	30/11/11 A	16/06/13	30/11/11 A	22/08/11	-664d	E&M0103, E&M0290	E&M0295, E&M0320, E&M0500, E&M3160					
Drawings Submission & Approval															
E&M0235	Sub. P&ID Drawings	100	75	24/06/10 A	24/05/13	24/06/10 A	31/07/11	-664d	E&M0010	E&M0250					
E&M0240	Sub. Plant GA Drawings	45	68	04/08/10 A	14/05/13	04/08/10 A	31/07/11	-653d	E&M0040	E&M0250, E&M0280, E&M0290					
E&M0250	Sub. Builder's Works Requirements Drawings	15	100	04/08/10 A	31/01/13 A	04/08/10 A	31/01/13 A		E&M0235, E&M0240, E&M0260,	E&M0280, E&M0290					
E&M0260	Sub. Mechanical Installation Drawings	60	70	27/09/10 A	17/05/13	27/09/10 A	31/07/11	-657d	E&M0040	E&M0250					
E&M0270	Sub. Electrical Installation Drawings	60	75	27/09/10 A	14/05/13	27/09/10 A	31/07/11	-654d	E&M0040	E&M0250, E&M0280					
E&M0280	Sub. BS Installation Drawings	120	95	27/09/10 A	30/05/13	27/09/10 A	18/04/12	-408d	E&M0240, E&M0250, E&M0270	E&M0220					
E&M0290	Sub. FS Installation Drawings	120	85	13/11/11 A	11/06/13	13/11/11 A	18/08/11	-664d	E&M0240, E&M0250	E&M0230					
Statutory Submission															
E&M0295	Preparation of Submission to HEC	39	100	01/11/11 A	30/11/11 A	01/11/11 A	30/11/11 A		E&M0080, E&M0230, E&M0430	E&M0300					
E&M0300	Application & Approval from HEC	150	90	01/11/11 A	01/07/13	01/11/11 A	04/11/12	-239d	E&M0295	E&M0305					
E&M0305	Provision of Cables to the STWs	180	0	01/07/13	28/12/13	05/11/12	03/05/13	-239d	E&M0300	E&M0680					
E&M0320	Form 314 Submission to FSD	14	0	16/06/13	30/06/13	20/04/13	03/05/13	-58d	E&M0230	E&M0325, E&M0670					
E&M0325	Submission to WSD	14	100	01/11/11 A	29/02/12 A	01/11/11 A	29/02/12 A		E&M0320	E&M0670, E&M0680					
E&M0330	Form 501 Submission to FSD (YSW)	28	0	11/03/15	08/04/15	14/11/13	11/12/13	-483d	E&M0500	E&M0700					
E&M0340	Form 501 Submission to FSD (SKW)	28	0	04/12/13	01/01/14	11/06/14	08/07/14	189d	E&M3160	E&M3360					
E&M0350	Form 501 Submission to FSD (PS1 & PS2)	28	0	28/05/13	25/06/13	14/11/12	11/12/12	-196d	E&M2016	E&M11800, E&M2180					
Yung Shue Wan															
Preliminary															
YSW0020	Approval of Environmental Team	16	100	17/05/10 A	01/06/10 A	17/05/10 A	01/06/10 A		KD0020	YSW00201, YSW0030, YSW00351,					
YSW00201	Change Baseline Monitoring Location (Air&Noise)	59	100	02/06/10 A	30/07/10 A	02/06/10 A	30/07/10 A		YSW0020	YSW0030					
YSW0030	Baseline monitoring (Air & Noise)	23	100	31/07/10 A	22/08/10 A	31/07/10 A	22/08/10 A		YSW0020, YSW00201	YSW0035					
YSW0035	Baseline Monitoring Report Submission (A & N)	16	100	23/08/10 A	07/09/10 A	23/08/10 A	07/09/10 A		YSW0030	YSW0120, YSW01545, YSW0500,					
YSW00351	Submission & Approval for Monitoring Method (W)	58	100	02/06/10 A	29/07/10 A	02/06/10 A	29/07/10 A		YSW0020	YSW0040					
YSW0040	Baseline monitoring (Water)	155	100	30/07/10 A	31/12/10 A	30/07/10 A	31/12/10 A		YSW0020, YSW00351	YSW0350					
YSW0050	Erect Hoarding and Fencing	60	100	19/05/10 A	17/07/10 A	19/05/10 A	17/07/10 A		KD0020	YSW0155					
Section W 1 - Slope Works in Portion A & C															
YSW0075	Mobilization	30	100	17/05/10 A	15/06/10 A	17/05/10 A	15/06/10 A		KD0020	YSW0080, YSW0100					
YSW0080	Site Clearance	30	100	16/06/10 A	15/07/10 A	16/06/10 A	15/07/10 A		YSW0075	YSW0085, YSW0090, YSW0120					
YSW0085	Initial Survey	14	100	02/07/10 A	15/07/10 A	02/07/10 A	15/07/10 A		YSW0080	YSW0120					
YSW0090	Verify the Rock Boulder required Stabilization Wk	249	100	16/07/10 A	21/03/11 A	16/07/10 A	21/03/11 A		YSW0080	YSW0100, YSW0110					
YSW0100	Removal of Rock Boulder	257	100	20/09/10 A	03/06/11 A	20/09/10 A	03/06/11 A		YSW0075, YSW0090	KD0030					
YSW0110	Stablizing work for rock boulder	35	100	16/07/11 A	19/08/11 A	16/07/11 A	19/08/11 A		YSW0090	KD0030					
YSW0120	Cut the slope to design profile	2	100	24/09/10 A	25/09/10 A	24/09/10 A	25/09/10 A		YSW0035, YSW0080, YSW0085	YSW0131, YSW0155, YSW0170					
YSW0131	Mobilization of Plant and Material of Soil Nails	14	100	12/09/10 A	25/09/10 A	12/09/10 A	25/09/10 A		YSW0120	YSW0132					
YSW0132	Erect Scaffold and Working Platform	2	100	26/09/10 A	27/09/10 A	26/09/10 A	27/09/10 A		YSW0131	YSW0133					
YSW0133	Setting out and Verify Locations of Soil Nails	45	100	28/09/10 A	11/11/10 A	28/09/10 A	11/11/10 A		YSW0132	YSW0134					
YSW0134	Drilling and Soil Nails Installation	43	100	19/10/10 A	30/11/10 A	19/10/10 A	30/11/10 A		YSW0133	YSW0135					
YSW0135	Construction of Nail Heads	12	100	01/12/10 A	12/12/10 A	01/12/10 A	12/12/10 A		YSW0134	YSW0136					
YSW0136	Mesh Installation on Cut Slope	3	100	13/12/10 A	15/12/10 A	13/12/10 A	15/12/10 A		YSW0135	YSW01361					
YSW01361	Verify alignment of access & channels on slope	118	100	16/12/10 A	12/04/11 A	16/12/10 A	12/04/11 A		YSW0136	YSW0140					
YSW0140	Construct U-channels & Step Channel on Cut Slope	182	100	13/04/11 A	11/10/11 A	13/04/11 A	11/10/11 A		YSW01361	KD0030					

Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	2A
c Primavera Systems, Inc.	

	Early bar
	Progress bar
	Critical bar
	Summary bar
	Progress point
	Critical point
	Summary point
	Start milestone point
	Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013				
											APR	MAY	JUN	JUL	
YSW0153	Removal of Ex U-Channel where clash with B. Wall	151	100	10/05/11 A	07/10/11 A	10/05/11 A	07/10/11 A		YSW01545	YSW01750					
YSW01545	Temporary Diversion of Drainage	244	100	08/09/10 A	09/05/11 A	08/09/10 A	09/05/11 A		YSW0035	YSW0153					
YSW0155	RC Barrier Wall Bay 1-13 (below Ground Level)	256	100	26/09/10 A	08/06/11 A	26/09/10 A	08/06/11 A		YSW0050, YSW0120	KD0030, YSW0170, YSW0175, YSW01750					
YSW0170	RC Barrier Wall Bay 1-13 (above Ground Level)	125	100	09/06/11 A	11/10/11 A	09/06/11 A	11/10/11 A		YSW0120, YSW0155	KD0030					
YSW0175	Construct U-channels and Catchpits (Phase 1)	76	100	09/06/11 A	23/08/11 A	09/06/11 A	23/08/11 A		YSW0155	KD0030					
YSW01750	Construction of subsoil drain (phase 1)	7	100	12/10/11 A	08/02/12 A	12/10/11 A	08/02/12 A		YSW0153, YSW0155	KD0030					
YSW01755	Construct subsoil drain (phase 2)	14	100	06/12/12 A	31/12/12 A	06/12/12 A	31/12/12 A		KD0030, YSW01800	KD0130					
YSW01800	RC Barrier Wall Bay 14 (below & above Ground)	87	100	03/09/12 A	28/11/12 A	03/09/12 A	28/11/12 A		YSW0760	YSW01755, YSW01810					
YSW01805	Hydroseeding	14	100	02/03/13 A	02/03/13 A	02/03/13 A	02/03/13 A		YSW01810	KD0130					
YSW01810	Construct U-channels and Catchpits (Phase 2)	30	100	29/11/12 A	22/12/12 A	29/11/12 A	22/12/12 A		YSW01800	KD0130, YSW01805					
Section W2 - YSW STW & Submarine Outfall															
Civil & Structural Work															
YSW0412	Mobilization	30	100	17/05/10 A	15/06/10 A	17/05/10 A	15/06/10 A		KD0020	YSW0422					
YSW0422	Site Clearance	30	100	17/05/10 A	15/06/10 A	17/05/10 A	15/06/10 A		KD0020, YSW0412	YSW0432, YSW0500, YSW0610, YSW0650					
YSW0432	Initial Survey	14	100	02/06/10 A	15/06/10 A	02/06/10 A	15/06/10 A		YSW0422	YSW0510					
YSW STW - GL H - T															
YSW0500	ELS & Excavation for Inlet Pumping Station	105	100	08/09/10 A	21/12/10 A	08/09/10 A	21/12/10 A		YSW0035, YSW0422	YSW0510					
YSW0510	Sub-structure construction (Inlet Pumping Stn)	129	100	22/12/10 A	29/04/11 A	22/12/10 A	29/04/11 A		YSW0432, YSW0500	YSW0520					
YSW0520	Backfill & Remove ELS (Inlet Pumping Stn)	40	100	30/04/11 A	08/06/11 A	30/04/11 A	08/06/11 A		YSW0510	YSW05701					
YSW0530	ELS & Excavation for Equalization Tank	159	100	01/01/11 A	08/06/11 A	01/01/11 A	08/06/11 A		YSW0660	YSW0540, YSW05701					
YSW0540	Sub-structure construction (Equalization Tank)	112	100	09/06/11 A	28/09/11 A	09/06/11 A	28/09/11 A		YSW0530	YSW0550, YSW05901					
YSW0550	Backfilling & Remove ELS (Equalization Tank)	20	100	29/09/11 A	18/10/11 A	29/09/11 A	18/10/11 A		YSW0540	YSW05901					
YSW05701	ELS & Excavation for Grit Chambers	28	100	09/06/11 A	06/07/11 A	09/06/11 A	06/07/11 A		YSW0520, YSW0530	YSW05711, YSW05731					
YSW05711	Construct sub-structure for Grit Chambers	106	100	07/07/11 A	20/10/11 A	07/07/11 A	20/10/11 A		YSW05701	YSW05721, YSW05911					
YSW05721	Backfill & Remove ELS for Grit Chambers	12	100	21/10/11 A	01/11/11 A	21/10/11 A	01/11/11 A		YSW05711	YSW05911					
YSW05731	ELS & Excavation for Grease Separators (GS)	34	100	07/07/11 A	09/08/11 A	07/07/11 A	09/08/11 A		YSW05701	YSW05741					
YSW05741	Construct sub-structure for Grease Separators	52	100	10/08/11 A	30/09/11 A	10/08/11 A	30/09/11 A		YSW05731	YSW05751					
YSW05751	Install Dia.400 Puddles in Grease Separators	27	100	01/10/11 A	27/10/11 A	01/10/11 A	27/10/11 A		YSW05741	YSW05752					
YSW05752	Construct sub-structure for GS (above puddles)	48	100	28/10/11 A	14/12/11 A	28/10/11 A	14/12/11 A		YSW05751	YSW05761					
YSW05761	Backfill & remove ELS for Grease Separators	10	100	15/12/11 A	24/12/11 A	15/12/11 A	24/12/11 A		YSW05752	YSW0580, YSW05921					
YSW0580	Excavate to Formation for Deodorizer Room	10	100	25/12/11 A	03/01/12 A	25/12/11 A	03/01/12 A		YSW05761	YSW05801, YSW05922					
YSW05801	Excavate to formation - Grid J-N/5-7	40	100	04/01/12 A	12/02/12 A	04/01/12 A	12/02/12 A		YSW0580	YSW05802, YSW05923					
YSW05802	Excavate to formation - Grid GA-H/5-7	10	100	13/02/12 A	22/02/12 A	13/02/12 A	22/02/12 A		YSW05801	YSW05924					
YSW05901	G/F to 1/F Construction Grid GA-K/1-5	90	100	29/09/11 A	27/12/11 A	29/09/11 A	27/12/11 A		YSW0540, YSW0550	YSW06001					
YSW05911	G/F to 1/F Construction Grid N-S/1-5	80	100	21/10/11 A	08/01/12 A	21/10/11 A	08/01/12 A		YSW05711, YSW05721	YSW06011, YSW06035					
YSW05921	G/F to 1/F Construction Grid K-N/1-5	45	100	25/12/11 A	07/02/12 A	25/12/11 A	07/02/12 A		YSW05761	YSW06021					
YSW05922	G/F to 1/F Construction for Deodorizer Room	80	100	04/01/12 A	23/03/12 A	04/01/12 A	23/03/12 A		YSW0580	YSW06022					
YSW05923	G/F to 1/F Construction for Grid J-N/5-7	60	100	13/02/12 A	12/04/12 A	13/02/12 A	12/04/12 A		YSW05801	E&M0530, E&M0540, E&M0550, E&M0560,					
YSW05924	G/F to 1/F Construction for Grid GA-H/5-7	50	100	28/05/12 A	16/07/12 A	28/05/12 A	16/07/12 A		YSW05802, YSW06023	YSW06034					
YSW06001	1/F to Roof Constuction for Grid GA-K/1-5	87	100	28/12/11 A	23/03/12 A	28/12/11 A	23/03/12 A		YSW05901	YSW0800					
YSW06011	1/F to Roof Constuction for Grid N-S/1-5	75	100	09/01/12 A	23/03/12 A	09/01/12 A	23/03/12 A		YSW05911	YSW0800					
YSW06021	1/F to Roof Constuction for Grid K-N/1-5	44	100	08/02/12 A	22/03/12 A	08/02/12 A	22/03/12 A		YSW05921	YSW07201					
YSW06022	1/F to Roof Constuction for Deodorizer Room	60	100	24/03/12 A	22/05/12 A	24/03/12 A	22/05/12 A		YSW05922	YSW0800					
YSW06023	1/F to Roof Constuction for Grid J-N/5-7	45	100	13/04/12 A	27/05/12 A	13/04/12 A	27/05/12 A		YSW05923	E&M0580, YSW05924					
YSW06034	1/F to Roof Constuction for Grid GA-H/5-7	28	100	27/07/12 A	13/08/12 A	27/07/12 A	13/08/12 A		YSW05924	YSW0800					
YSW06035	Construct baffle walls in Grease Separators	90	100	18/04/12 A	16/07/12 A	18/04/12 A	16/07/12 A		YSW05911	YSW07204					
YSW07201	Water tightness test for Inlet Pumping Station	60	100	23/03/12 A	21/05/12 A	23/03/12 A	21/05/12 A		YSW06021	YSW07202, YSW0800					
YSW07202	Water tightness test for Equalization Tanks	42	100	22/05/12 A	02/07/12 A	22/05/12 A	02/07/12 A		YSW07201	E&M0600, YSW07203, YSW0800					
YSW07203	Water tightness test for Grit Chambers	42	100	17/09/12 A	29/09/12 A	17/09/12 A	29/09/12 A		YSW07202	YSW07204, YSW0800					
YSW07204	Water tightness test for Grease Separators	32	100	03/10/12 A	31/10/12 A	03/10/12 A	31/10/12 A		YSW06035, YSW07203	E&M0570, YSW07205, YSW0800					
YSW07205	Water tightness test for water channels	21	0	30/04/13	23/05/13	07/06/14	30/06/14	403d	YSW07204	YSW0800					
YSW0800	ABWF installation	271	94	03/07/12 A	16/05/13	03/07/12 A	16/06/14	397d	YSW06001, YSW06011, YSW06022,	KD0040					
YSW STW - GL T - X															
YSW0610	Excavate to formation	10	100	08/09/10 A	17/09/10 A	08/09/10 A	17/09/10 A		YSW0035, YSW0422	YSW0620					
YSW0620	Base slab construction	248	100	18/09/10 A	23/05/11 A	18/09/10 A	23/05/11 A		YSW0610	YSW0630					
YSW0630	G/F to 1/F construction	205	100	24/05/11 A	14/12/11 A	24/05/11 A	14/12/11 A		YSW0620	YSW0640					

Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	3A
c Primavera Systems, Inc.	

	Early bar
	Progress bar
	Critical bar
	Summary bar
	Progress point
	Critical point
	Summary point
	Start milestone point
	Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013				
											APR	MAY	JUN	JUL	
YSW0640	1/F to Roof Construction	64	100	15/12/11 A	16/02/12 A	15/12/11 A	16/02/12 A		YSW0630	YSW0810					
YSW0810	ABWF installation	80	100	28/12/11 A	16/03/12 A	28/12/11 A	16/03/12 A		YSW0640	E&M0610, E&M0620, E&M0630, E&M0640					
YSW STW - GL F - H & DN Tanks															
YSW0650	ELS & Excavation for DN Tanks	37	100	08/09/10 A	14/10/10 A	08/09/10 A	14/10/10 A		YSW0035, YSW0422	YSW0660					
YSW0660	Sub-structure construction (DN Tanks)	78	100	15/10/10 A	31/12/10 A	15/10/10 A	31/12/10 A		YSW0650	YSW0530, YSW0670					
YSW0670	Backfill & Remove ELS (DN Tanks)	70	100	01/01/11 A	11/03/11 A	01/01/11 A	11/03/11 A		YSW0660	YSW0680					
YSW0680	Base slab construction (SD1, SD2 & MBR4)	17	100	12/03/11 A	28/03/11 A	12/03/11 A	28/03/11 A		YSW0670	YSW0690					
YSW0690	Construct Superstructure SD1, SD2 & MBR4	82	100	29/03/11 A	18/06/11 A	29/03/11 A	18/06/11 A		YSW0680	YSW0710, YSW0820					
YSW06901	Construct Superstructure of DN Tanks	28	100	15/05/12 A	11/06/12 A	15/05/12 A	11/06/12 A		YSW0735	YSW0830					
YSW0705	Water test for MBR 4	47	100	01/10/12 A	16/11/12 A	01/10/12 A	16/11/12 A		YSW0710	E&M0510, E&M0640, YSW07055, YSW0820					
YSW07055	Water test for SD1 & SD2	54	100	17/11/12 A	10/01/13 A	17/11/12 A	10/01/13 A		YSW0705, YSW07105	E&M0610					
YSW0710	Apply protective paint for MBR 4	7	100	24/09/12 A	30/09/12 A	24/09/12 A	30/09/12 A		YSW0690	YSW0705, YSW07105					
YSW07105	Apply protective paint for SD1 & SD2	7	100	01/10/12 A	07/10/12 A	01/10/12 A	07/10/12 A		YSW0710	YSW07055					
YSW0820	ABWF installation	34	35	15/01/13 A	21/05/13	15/01/13 A	15/01/13	-126d	YSW0690, YSW0705	E&M0630, E&M0640					
YSW0830	Water test for DN Tanks	28	0	30/04/13	27/05/13	18/02/13	18/03/13	-70d	YSW06901	YSW0850					
YSW0850	Apply protective paint for DN Tanks	6	10	27/04/13 A	01/06/13	27/04/13 A	23/03/13	-70d	YSW0830	E&M0610					
YSW STW - GL A - F															
YSW0730	Completion of HDD	0	100	21/01/12 A		21/01/12 A			YSW03601, YSW03605	YSW0732					
YSW0732	Excavate for MBR 2 & 3	20	100	21/01/12 A	09/02/12 A	21/01/12 A	09/02/12 A		YSW0730	YSW0733					
YSW0733	Construct basement of MBR 2 & 3	20	100	10/02/12 A	29/02/12 A	10/02/12 A	29/02/12 A		YSW0732	YSW0735, YSW0740					
YSW0735	Construct superstructure of MBR 2	75	100	01/03/12 A	14/05/12 A	01/03/12 A	14/05/12 A		YSW0733	YSW06901, YSW0736, YSW08302,					
YSW0736	Construct superstructure of MBR 3	100	100	15/05/12 A	14/05/12 A	15/05/12 A	14/05/12 A		YSW0735	YSW08302, YSW08305					
YSW0740	ELS & excavate for Outfall Shaft	75	100	01/03/12 A	14/05/12 A	01/03/12 A	14/05/12 A		YSW0733	YSW0750					
YSW0750	Construct basement of Outfall Shaft	19	100	15/05/12 A	02/06/12 A	15/05/12 A	02/06/12 A		YSW0740	YSW07501					
YSW07501	Connect additional flange to HDPE pipe (VO 042)	5	100	03/06/12 A	07/06/12 A	03/06/12 A	07/06/12 A		YSW0750	YSW07502					
YSW07502	Construct sub-structure of Outfall Shaft	16	100	08/06/12 A	23/06/12 A	08/06/12 A	23/06/12 A		YSW07501	YSW0760					
YSW0760	Backfill & remove ELS (outfall shaft)	8	100	24/06/12 A	01/07/12 A	24/06/12 A	01/07/12 A		YSW07502	YSW01800, YSW07601, YSW07603,					
YSW07601	Construct superstructure for Outfall Shaft	30	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		YSW0760	YSW08301, YSW08305					
YSW07603	ELS & excavate for FSH Water Supply Tank	25	100	01/06/12 A	25/06/12 A	01/06/12 A	25/06/12 A		YSW0760	YSW07604					
YSW07604	Construct substructure for FSH Water Supply Tank	24	100	26/06/12 A	19/07/12 A	26/06/12 A	19/07/12 A		YSW07603	YSW07605					
YSW07605	Backfill & remove ELS for FSH Water Supply Tank	12	100	20/07/12 A	31/07/12 A	20/07/12 A	31/07/12 A		YSW07604	YSW07607					
YSW07607	Construct basement of MBR 1 & Workshop	24	100	01/08/12 A	24/08/12 A	01/08/12 A	24/08/12 A		YSW07605	YSW07608, YSW07609					
YSW07608	Construct superstructure for FSH Water Supply Tk	37	100	25/08/12 A	30/09/12 A	25/08/12 A	30/09/12 A		YSW07607	YSW08304, YSW08305					
YSW07609	Construct superstructure for MBR 1	37	100	25/08/12 A	30/09/12 A	25/08/12 A	30/09/12 A		YSW07607	YSW07610, YSW08303, YSW1470					
YSW07610	Construct Workshop, FSSH Pump Rm, PW Pump Rm	31	100	03/10/12 A	31/10/12 A	03/10/12 A	31/10/12 A		YSW07609	YSW0840, YSW16606, YSW16607,					
YSW08301	Water tightness test for Outfall Shaft	42	100	03/04/13 A	18/04/13 A	03/04/13 A	18/04/13 A		YSW0380, YSW07601	E&M0690					
YSW08302	Water tightness test for MBR 2 & 3	95	100	03/07/12 A	05/10/12 A	03/07/12 A	05/10/12 A		YSW0735, YSW0736	E&M0520, E&M0590, E&M0605, E&M0650					
YSW08303	Water tightness test for MBR 1	19	100	30/11/12 A	18/12/12 A	30/11/12 A	18/12/12 A		YSW07609	E&M0520					
YSW08304	Water tightness test for FSH Water Supply Tank	32	0	30/04/13	31/05/13	19/02/13	23/03/13	-69d	YSW07608	E&M0610					
YSW08305	Apply protective paint	120	80	02/10/12 A	23/05/13	02/10/12 A	23/03/13	-61d	YSW0735, YSW0736, YSW07601,	E&M0610, YSW0870					
YSW0870	ABWF installation	30	0	24/05/13	22/06/13	18/05/14	16/06/14	359d	YSW08305	KD0040					
Fire Hose Reel / Sprinkler Pump Rm															
YSW0840	ELS & excavate to formation (+0 mPD approx.)	40	100	25/02/13 A	18/04/13 A	25/02/13 A	18/04/13 A		YSW07610, YSW16606	YSW0860					
YSW0860	Sub-structure construction	40	80	19/04/13 A	12/05/13	19/04/13 A	18/05/13	7d	YSW0840	YSW0890					
YSW0880	Backfill & remove ELS	35	0	21/06/13	26/07/13	25/11/16	13/01/17	1185d	YSW0890						
YSW0890	Construction Ground Slab at +5.2mPD	40	0	12/05/13	21/06/13	19/05/13	27/06/13	7d	YSW0860	YSW0880, YSW0900					
YSW0900	Superstructure construction upto +9.2mPD	35	0	21/06/13	26/07/13	28/06/13	01/08/13	7d	YSW0890	YSW0910, YSW0925					
YSW0910	Water test	28	0	26/07/13	23/08/13	02/08/13	29/08/13	7d	YSW0900	YSW0915					
YSW0915	Apply protective paint	14	0	23/08/13	06/09/13	30/08/13	12/09/13	7d	YSW0910	E&M0640, YSW0925					
YSW0925	ABWF installation	30	0	07/08/13	06/09/13	18/05/14	16/06/14	284d	YSW0900, YSW0915	KD0040					
Emergency Storage Tank															
YSW1470	ELS & excavate to formation (-1.5mPD Approx.)	16	100	17/09/12 A	02/10/12 A	17/09/12 A	02/10/12 A		YSW07609	YSW1480					
YSW1480	Sub-structure construction	14	100	03/10/12 A	16/10/12 A	03/10/12 A	16/10/12 A		YSW1470	YSW1490					
YSW1490	Backfill & extract sheetpile	3	100	17/10/12 A	19/10/12 A	17/10/12 A	19/10/12 A		YSW1480	YSW1500					
YSW1500	Superstructure construction upto +10.5mPD	41	100	20/10/12 A	29/11/12 A	20/10/12 A	29/11/12 A		YSW1490	YSW1530, YSW1536					

Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	4A
© Primavera Systems, Inc.	

■	Early bar
■	Progress bar
■	Critical bar
■	Summary bar
▲	Progress point
▲	Critical point
▲	Summary point
▲	Start milestone point
▲	Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013				
											APR	MAY	JUN	JUL	
YSW1530	Underground pipeline works	40	0	30/04/13	08/06/13	21/04/13	30/05/13	-9d	YSW1500	E&M0690, YSW1680	Underground pipeline works				
YSW1536	Water tightness test	40	0	30/04/13	08/06/13	20/03/13	28/04/13	-41d	YSW1500	YSW1538	Water tightness test				
YSW1538	Apply protective paint	30	100	04/03/13 A	05/03/13 A	04/03/13 A	05/03/13 A		YSW1536	YSW1540					
YSW1540	ABWF installation	40	20	03/04/13 A	10/07/13	03/04/13 A	30/05/13	-41d	YSW1538	E&M0690	ABWF installation				
Road, Drain, Cable Draw Pits & Ducting															
YSW16601	ELS & excavate 6m deep sewer (FM1 - YFMH13)	60	0	04/05/13	03/07/13	19/01/13	19/03/13	-106d	YSW0760, YSW16606, YSW16607,	YSW16602	ELS & excavate 6m deep sewer				
YSW16602	Lay pipe & backfill 6m deep sewer (FM1 - YFMH13)	45	0	03/07/13	17/08/13	20/03/13	03/05/13	-106d	YSW16601	E&M0680, YSW1700	Lay pipe & backfill 6m deep sewer				
YSW16603	Construct UU & pipes along sea side (Grid Q-X)	60	0	03/05/13	02/07/13	24/03/13	22/05/13	-41d	YSW16607, YSW16608	YSW16604, YSW16703	Construct UU & pipes along sea side (Grid Q-X)				
YSW16604	Construct UU & pipes along sea side (Grid XA-D)	60	0	02/07/13	31/08/13	23/05/13	21/07/13	-41d	YSW16603	YSW16605, YSW16701	Construct UU & pipes along sea side (Grid XA-D)				
YSW16605	Construct UU & pipes along sea side (Grid D-Q)	60	0	31/08/13	30/10/13	22/07/13	19/09/13	-41d	YSW16604	YSW16702, YSW1700	Construct UU & pipes along sea side (Grid D-Q)				
YSW16606	Construct UU & pipes along hill side (Grid D-Q)	90	95	10/10/12 A	04/05/13	10/10/12 A	18/01/13	-106d	YSW07610	YSW0840, YSW16601	Construct UU & pipes along hill side (Grid D-Q)				
YSW16607	Construct UU & pipes along hill side (Grid Q-X)	72	95	20/08/12 A	03/05/13	20/08/12 A	18/01/13	-105d	YSW07610	YSW16601, YSW16603	Construct UU & pipes along hill side (Grid Q-X)				
YSW16608	Construct UU & pipes along hill side (Grid XA-D)	72	95	30/11/12 A	03/05/13	30/11/12 A	18/01/13	-105d	YSW07610	YSW16601, YSW16603, YSW1690	Construct UU & pipes along hill side (Grid XA-D)				
YSW16701	Construct Boundary Wall (Grid XA-D)	80	90	10/01/13 A	08/09/13	10/01/13 A	19/09/13	11d	YSW16604	YSW16702	Construct Boundary Wall (Grid XA-D)				
YSW16702	Construct Boundary Wall (Grid D-Q)	80	0	30/10/13	18/01/14	20/09/13	08/12/13	-41d	YSW16605, YSW16701	YSW16703	Construct Boundary Wall (Grid D-Q)				
YSW16703	Construct Boundary Wall (Grid Q-X)	80	0	18/01/14	08/04/14	09/12/13	26/02/14	-41d	YSW16603, YSW16702	YSW16704, YSW1700	Construct Boundary Wall (Grid Q-X)				
YSW16704	ABWF installation for Boundary Wall	240	0	30/10/13	27/06/14	20/10/13	16/06/14	-11d	YSW16703	KD0040	ABWF installation for Boundary Wall				
YSW1680	Fire Hydrant & pipeline installation	120	10	26/01/13 A	24/09/13	26/01/13 A	14/10/13	20d	YSW1530	YSW1690, YSW1700	Fire Hydrant & pipeline installation				
YSW1690	Construction of Road Kerbs, Downpipes, U-channel	180	25	02/01/13 A	06/02/14	02/01/13 A	26/02/14	20d	YSW16608, YSW1680	YSW1700	Construction of Road Kerbs, Downpipes, U-channel				
YSW1700	Road Paving	110	0	08/04/14	27/07/14	27/02/14	16/06/14	-41d	YSW16602, YSW16605, YSW16703, YSW1680, YSW1690	KD0040	Road Paving				
Submarine Outfall															
YSW0180	Coordination of HEC	53	100	17/05/10 A	08/07/10 A	17/05/10 A	08/07/10 A		KD0020	YSW0350	Coordination of HEC				
YSW0200	Submission and Approval of Ecologist	60	100	17/05/10 A	15/07/10 A	17/05/10 A	15/07/10 A		KD0020	YSW0210	Submission and Approval of Ecologist				
YSW0210	Ecology Survey	211	100	16/07/10 A	11/02/11 A	16/07/10 A	11/02/11 A		YSW0200	YSW0350	Ecology Survey				
YSW0220	Submission and Approval of In. Hydro Survey	103	100	17/05/10 A	27/08/10 A	17/05/10 A	27/08/10 A		KD0020	YSW0230	Submission and Approval of In. Hydro Survey				
YSW0230	Hydrographical Survey (YSW)	157	100	28/08/10 A	31/01/11 A	28/08/10 A	31/01/11 A		YSW0220	YSW0350	Hydrographical Survey (YSW)				
YSW0240	Material Submission, Approval of HDPE pipe	319	100	17/05/10 A	31/03/11 A	17/05/10 A	31/03/11 A		KD0020	YSW0360	Material Submission, Approval of HDPE pipe				
YSW02401	Clarify Coordinate of Point Y (Reply of RFI 010)	83	100	28/06/10 A	18/09/10 A	28/06/10 A	18/09/10 A		KD0020	YSW0250	Clarify Coordinate of Point Y (Reply of RFI 010)				
YSW0250	Submit and Approval of Method Statement for HDD	188	100	19/09/10 A	25/03/11 A	19/09/10 A	25/03/11 A		YSW02401	YSW0260, YSW0270, YSW0340	Submit and Approval of Method Statement for HDD				
YSW0260	Submission of HDD Method Statement to HEC	14	100	26/03/11 A	08/04/11 A	26/03/11 A	08/04/11 A		YSW0250	YSW0340	Submission of HDD Method Statement to HEC				
YSW0270	Additional G.I. Boreholes (YSW)	123	100	19/09/10 A	19/01/11 A	19/09/10 A	19/01/11 A		YSW0250	YSW0280, YSW0290	Additional G.I. Boreholes (YSW)				
YSW0280	Submission of propose alignment	44	100	20/01/11 A	04/03/11 A	20/01/11 A	04/03/11 A		YSW0270	YSW0310, YSW0340	Submission of propose alignment				
YSW0290	Submission of Marine Notice	69	100	20/01/11 A	29/03/11 A	20/01/11 A	29/03/11 A		YSW0270	YSW0350	Submission of Marine Notice				
YSW0310	Construction of Entry Pit and Preparation Work	27	100	05/03/11 A	31/03/11 A	05/03/11 A	31/03/11 A		YSW0280	YSW0320	Construction of Entry Pit and Preparation Work				
YSW0320	Prepare of HDD Drill Rig Set-up (YSW)	28	100	01/04/11 A	28/04/11 A	01/04/11 A	28/04/11 A		YSW0310	YSW0330, YSW0350	Prepare of HDD Drill Rig Set-up (YSW)				
YSW0330	Establishment of HDD plant & equipment	6	100	09/04/11 A	14/04/11 A	09/04/11 A	14/04/11 A		YSW0320	YSW0340	Establishment of HDD plant & equipment				
YSW0340	Setting up at drillhole location	14	100	15/04/11 A	28/04/11 A	15/04/11 A	28/04/11 A		YSW0250, YSW0260, YSW0280,	YSW0350	Setting up at drillhole location				
YSW0350	Drill pilot hole and reaming hole - NS400 - 530m	229	100	29/04/11 A	13/12/11 A	29/04/11 A	13/12/11 A		YSW0040, YSW0180, YSW0210,	YSW0360	Drill pilot hole and reaming hole - NS400 - 530m				
YSW0360	Installation of NS400 HDPE 530m	17	100	14/12/11 A	30/12/11 A	14/12/11 A	30/12/11 A		YSW0240, YSW0350	SKW1181, YSW03601, YSW03620,	Installation of NS400 HDPE 530m				
YSW03601	Demobilization of HDD plant & equipment	7	100	31/12/11 A	06/01/12 A	31/12/11 A	06/01/12 A		YSW0360	YSW03605, YSW03641, YSW0730	Demobilization of HDD plant & equipment				
YSW03605	Remove Entry pit of HDD	14	100	07/01/12 A	20/01/12 A	07/01/12 A	20/01/12 A		YSW03601	YSW0730	Remove Entry pit of HDD				
YSW03620	Removal of Receiving Pit	14	100	31/12/11 A	13/01/12 A	31/12/11 A	13/01/12 A		YSW0360	YSW0365	Removal of Receiving Pit				
YSW03641	Prepare backfilling material under VO 046A	120	100	07/01/12 A	05/05/12 A	07/01/12 A	05/05/12 A		YSW03601	YSW0365	Prepare backfilling material under VO 046A				
YSW0365	Set up of Silt Curtain as per EP	2	100	23/11/12 A	24/11/12 A	23/11/12 A	24/11/12 A		SKW1431, YSW03620, YSW03641	YSW0370	Set up of Silt Curtain as per EP				
YSW0370	Dredging of Marine Deposit for Diffuser (YSW)	5	100	24/11/12 A	29/11/12 A	24/11/12 A	29/11/12 A		YSW0360, YSW0365	YSW0380	Dredging of Marine Deposit for Diffuser (YSW)				
YSW0380	Diffuser Construction (YSW)	60	65	30/11/12 A	20/05/13	30/11/12 A	30/05/13	10d	YSW0370	E&M0690, YSW0400, YSW08301	Diffuser Construction (YSW)				
YSW0400	Removal of silt curtain	30	0	21/05/13	19/06/13	18/05/14	16/06/14	362d	YSW0380	KD0040	Removal of silt curtain				
E&M Works - YSW STW															
E&M0360	Delivery of MBR Memb. Mod. (MBR Tk 4)	118	100	24/02/11 A	21/06/11 A	24/02/11 A	21/06/11 A		E&M0160	E&M0510	Delivery of MBR Memb. Mod. (MBR Tk 4)				
E&M0370	Delivery of MBR Membrane Modules - 2nd Shipment	236	100	24/02/11 A	17/10/11 A	24/02/11 A	17/10/11 A		E&M0160	E&M0520	Delivery of MBR Membrane Modules - 2nd Shipment				
E&M0380	Delivery of Grit Removal Equipment	81	100	10/10/11 A	29/12/11 A	10/10/11 A	29/12/11 A		E&M0150	E&M0530	Delivery of Grit Removal Equipment				
E&M0390	Delivery of Coarse Screens	129	100	06/09/11 A	12/01/12 A	06/09/11 A	12/01/12 A		E&M0110	E&M0540	Delivery of Coarse Screens				
E&M0400	Delivery of Fine Screens	80	100	12/09/11 A	30/11/11 A	12/09/11 A	30/11/11 A		E&M0120	E&M0550	Delivery of Fine Screens				
E&M0410	Delivery of Pumps	75	100	23/06/11 A	05/09/11 A	23/06/11 A	05/09/11 A		E&M0130	E&M0560	Delivery of Pumps				
E&M0420	Delivery of Submersible Mixers	230	100	26/02/11 A	26/02/11 A	26/02/11 A	26/02/11 A		E&M0140	E&M0570	Delivery of Submersible Mixers				

Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	5A
© Primavera Systems, Inc.	

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ▲ Progress point
- ▲ Critical point
- ▲ Summary point
- ▲ Start milestone point
- ▲ Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013			
											APR	MAY	JUN	JUL
E&M0440	Delivery of Sludge Dewatering Equipment	558	70	31/08/11 A	14/10/13	31/08/11 A	10/08/13	-65d	E&M0170	E&M0580				
E&M0450	Delivery of Valves, Pipes & Fittings	560	90	30/08/11 A	26/11/13	30/08/11 A	07/11/13	-19d	E&M0180	E&M0590				
E&M0460	Delivery of Penstocks	135	100	12/08/11 A	24/12/11 A	12/08/11 A	24/12/11 A		E&M0190	E&M0600, E&M0605				
E&M0470	Delivery of Instruments	232	100	03/11/11 A	21/06/11 A	03/11/11 A	21/06/11 A		E&M0200	E&M0610				
E&M0480	Delivery of MCC LVSB	90	100	03/12/12 A	04/03/15 A	03/12/12 A	04/03/15 A		E&M0210	E&M0620				
E&M0490	Delivery of BS Equipment	446	65	10/12/11 A	18/07/14	10/12/11 A	05/06/13	-408d	E&M0220	E&M0630				
E&M0500	Delivery FS Equipment	507	25	11/12/11 A	11/03/15	11/12/11 A	16/05/13	-664d	E&M0230	E&M0330, E&M0640				
E&M0510	Install Membrane Modules in MBR Tank no. 4	89	100	03/11/12 A	28/02/13 A	03/11/12 A	28/02/13 A		E&M0360, YSW0705	E&M0690				
E&M0520	Install Membrane Modules in MBR Tank No. 1 to 3	57	100	03/12/12 A	28/02/13 A	03/12/12 A	28/02/13 A		E&M0370, YSW08302, YSW08303	E&M0690				
E&M0530	Install Grit Removal Equipment	122	100	01/06/12 A	30/09/12 A	01/06/12 A	30/09/12 A		E&M0380, YSW05923	E&M0590, E&M0660				
E&M0540	Install Coarse Screens	240	90	23/04/12 A	23/05/13	23/04/12 A	22/04/13	-31d	E&M0390, YSW05923	E&M0660				
E&M0550	Install Fine Screens	122	80	01/06/12 A	24/05/13	01/06/12 A	12/03/13	-73d	E&M0400, YSW05923	E&M0590, E&M0660				
E&M0560	Install Pumps	355	60	23/04/12 A	18/09/13	23/04/12 A	22/04/13	-149d	E&M0410, YSW05923	E&M0660				
E&M0570	Install Submersible Mixers	163	50	15/01/13 A	20/07/13	15/01/13 A	22/04/13	-89d	E&M0420, YSW07204	E&M0660, E&M0690				
E&M0580	Install Sludge Dewatering Equipment	361	40	29/05/12 A	02/12/13	29/05/12 A	31/05/13	-185d	E&M0440, YSW06023	E&M0690				
E&M0590	Install Valves, Pipes & Fittings	232	65	15/01/13 A	13/08/13	15/01/13 A	01/06/13	-73d	E&M0450, E&M0530, E&M0550,	E&M0650, E&M0690				
E&M0600	Install Penstocks (Batch 1, GL H - T)	213	100	23/04/12 A	21/05/13 A	23/04/12 A	21/05/13 A		E&M0460, YSW07202	E&M0690				
E&M0605	Install Penstocks (Batch 2, GL A - F)	131	70	02/01/13 A	08/06/13	02/01/13 A	30/05/13	-8d	E&M0460, YSW08302	E&M0690				
E&M0610	Install Instruments	74	5	02/01/13 A	11/08/13	02/01/13 A	01/06/13	-70d	E&M0470, YSW07055, YSW0810,	E&M0690				
E&M0620	Install SAT, MCC & LVSB	8	100	02/01/13 A	02/01/15 A	02/01/13 A	02/01/15 A		E&M0480, YSW0810	E&M0660, E&M0690				
E&M0630	Install BS Equipment	180	50	02/01/13 A	17/08/14	02/01/13 A	05/07/13	-408d	E&M0490, YSW0810, YSW0820	E&M0690				
E&M0640	Install FS Equipment	180	5	02/01/13 A	30/04/15	02/01/13 A	05/07/13	-664d	E&M0500, YSW0705, YSW0810,	E&M0690				
E&M0650	Hydraulic Tests of Pipeworks	153	30	02/01/13 A	15/08/13	02/01/13 A	06/06/13	-69d	E&M0590, YSW08302	E&M0690				
E&M0660	Cabling Works	15	20	04/02/15 A	12/01/15	04/02/15 A	04/05/13	-618d	E&M0530, E&M0540, E&M0550, E&M0560, E&M0570, E&M0620	E&M0670				
E&M0670	Insulation Tests of Cables and Cable Termination	26	0	12/01/15	07/02/15	05/05/13	30/05/13	-618d	E&M0320, E&M0325, E&M0660,	E&M0690				
E&M0680	Energization	1	0	31/12/14 *	01/01/15	04/05/13	04/05/13	-607d	E&M0305, E&M0325, E&M0620,	E&M0670				
E&M0690	Functional and Performance Tests of Equipment	35	20	25/03/15 A	22/04/15	25/03/15 A	27/06/13 *	-664d	E&M0510, E&M0520, E&M0570, E&M0580, E&M0590, E&M0600, E&M0605, E&M0610, E&M0630, E&M0640, E&M0650, E&M0670, YSW0380, YSW08301, YSW1530, YSW1540	E&M0700				
E&M0700	T&C Period	137	0	22/04/15	06/09/15	12/12/13	27/04/14	-497d	E&M0330, E&M0690	E&M0730, KD0040				
E&M0730	Trial Operation Period	413	0	06/09/15	13/01/17	28/04/14	14/06/15	-497d	E&M0700	KD0132				

Sok Kwu Wan

Preliminary														
SKW0250	Approval of Environmental Team	16	100	17/05/10 A	01/06/10 A	17/05/10 A	01/06/10 A		KD0020	SKW0260				
SKW0260	Baseline monitoring (Air & Noise)	14	100	02/06/10 A	15/06/10 A	02/06/10 A	15/06/10 A		SKW0250	SKW0242, SKW0265, SKW0592, SKW0681,				
SKW0265	Baseline Monitoring Submission (A & N)	14	100	16/06/10 A	08/07/10 A	16/06/10 A	08/07/10 A		SKW0260	SKW0242, SKW0592, SKW0681, SKW0921,				
Section W 3 - Footpath Diversion in Portion G														
Civil & Geotechnical Works														
SKW0240	Site Clearance	21	100	17/05/10 A	06/06/10 A	17/05/10 A	06/06/10 A			SKW0241				
SKW0241	Initial Survey	9	100	07/06/10 A	15/06/10 A	07/06/10 A	15/06/10 A		SKW0240	SKW0242				
SKW0242	Retaining Wall Bay 0-10 (Incl. VO. 001A)	177	100	30/06/10 A	23/12/10 A	30/06/10 A	23/12/10 A		SKW0241, SKW0260, SKW0265	SKW0461				
SKW0461	Utilities Laying and Diversion	70	100	24/12/10 A	03/03/11 A	24/12/10 A	03/03/11 A		SKW0242	SKW0471				
SKW0471	Concreting for Pavement	7	100	04/03/11 A	10/03/11 A	04/03/11 A	10/03/11 A		SKW0461	SKW0481				
SKW0481	Footpath Diversion - Stage 1	14	100	11/03/11 A	24/03/11 A	11/03/11 A	24/03/11 A		SKW0471	KD0050, SKW04811, SKW0491				
SKW04811	Excavate for FP transition at CH0-35 & CH130-141	37	100	25/03/11 A	30/04/11 A	25/03/11 A	30/04/11 A		SKW0481	SKW04821				
SKW04821	Construction of Drainage outfall near bay 10	3	100	01/05/11 A	03/05/11 A	01/05/11 A	03/05/11 A		SKW04811	SKW04831				
SKW04831	Cable diversion by HEC	26	100	04/05/11 A	29/05/11 A	04/05/11 A	29/05/11 A		SKW04821	SKW04841				
SKW04841	Diversion of Ducting and Drawpit by PCCW	12	100	20/05/11 A	31/05/11 A	20/05/11 A	31/05/11 A		SKW04831	SKW04851				
SKW04851	Soil backfilling behind FP retaining wall	14	100	01/06/11 A	14/06/11 A	01/06/11 A	14/06/11 A		SKW04841	SKW04861				
SKW04861	Concreting for footpath pavement	7	100	15/06/11 A	21/06/11 A	15/06/11 A	21/06/11 A		SKW04851	SKW04871				
SKW04871	Relocation of Temp Safety Fence at SKW STW A-G	57	100	22/06/11 A	17/08/11 A	22/06/11 A	17/08/11 A		SKW04861	SKW04881				
SKW04881	Disposal of excavation material at A-G SKW STW	138	100	18/08/11 A	02/01/12 A	18/08/11 A	02/01/12 A		SKW04871	SKW04885				
SKW04885	Footpath Diversion - Stage 2	7	100	03/01/12 A	09/01/12 A	03/01/12 A	09/01/12 A		SKW04881	SKW1261				
SKW0491	Removal of Haul Road after SKW STW	7	0	08/10/14	14/10/14	29/05/15	04/06/15	233d	KD0090, SKW0481, SKW1401	SKW0501				

Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	6A
© Primavera Systems, Inc.	

	Early bar
	Progress bar
	Critical bar
	Summary bar
	Progress point
	Critical point
	Summary point
	Start milestone point
	Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013				
											APR	MAY	JUN	JUL	
SKW0501	Concreting for no-fine concrete	14	0	08/10/14	21/10/14	29/05/15	11/06/15	233d	SKW0491	SKW0511					
SKW0511	Wall Tie & Stone Facing	14	0	22/10/14	04/11/14	12/06/15	25/06/15	233d	SKW0501	SKW0521					
SKW0521	Gabion Wall & Geotextile	30	0	05/11/14	04/12/14	26/06/15	25/07/15	233d	SKW0511	SKW0531					
SKW0531	Installation of Flower Pot	7	0	05/12/14	11/12/14	26/07/15	01/08/15	233d	SKW0521	SKW0541					
SKW0541	Completion of Outstanding Works	42	0	12/12/14	22/01/15	02/08/15	12/09/15	233d	SKW0531	KD0125					
Section W 4 - Slope Works in Portions H & I															
Geotechnical Works															
SKW0588	Construct scaffolding access	30	100	15/06/10 A	14/07/10 A	15/06/10 A	14/07/10 A		KD0020	SKW0590					
SKW0590	Site Clearance for Slope	100	100	15/07/10 A	22/10/10 A	15/07/10 A	22/10/10 A		SKW0588	SKW0591					
SKW0591	Initial Survey for Slope	28	100	21/09/10 A	18/10/10 A	21/09/10 A	18/10/10 A		SKW0590	SKW0592					
SKW0592	Temporary Rockfall fence at ex. Footpath	43	100	31/08/10 A	12/10/10 A	31/08/10 A	12/10/10 A		SKW0260, SKW0265, SKW0591	SKW05931					
SKW05931	Construction of Haul Road (To +30mPD)	50	100	03/09/10 A	22/10/10 A	03/09/10 A	22/10/10 A		SKW0592	SKW05932					
SKW05932	Construction of Haul Road (To +42.5mPD)	68	100	23/10/10 A	29/12/10 A	23/10/10 A	29/12/10 A		SKW05931	SKW059322					
SKW059321	Removal of Boulders (IBG 1 - 119, SI No. 11B)	121	100	03/11/10 A	03/03/11 A	03/11/10 A	03/03/11 A			SKW059411					
SKW059322	Add. Site Invest. Works (VO. No. 9,12 &16)	174	100	11/01/11 A	03/07/11 A	11/01/11 A	03/07/11 A		SKW05932	SKW059341					
SKW059323	Revised Profile at West Slope (+56 to +42.5mPD)	1	100	17/03/11 A	17/03/11 A	17/03/11 A	17/03/11 A			SKW059324					
SKW059324	Construction of Haul Road (+42.5 to +56mPD)	12	100	18/03/11 A	29/03/11 A	18/03/11 A	29/03/11 A		SKW059323	SKW059325					
SKW059325	Removal of Boulders (IBG 120-139, SI No. 11C)	17	100	30/03/11 A	15/04/11 A	30/03/11 A	15/04/11 A		SKW059324	SKW05933					
SKW05933	West Slope Cutting (+56mPD to +42.5mPD)	2	100	16/04/11 A	17/04/11 A	16/04/11 A	17/04/11 A		SKW059325	SKW059331					
SKW059331	Removal of Boulders (IBG 140-189, SI No. 11D)	45	100	18/04/11 A	01/06/11 A	18/04/11 A	01/06/11 A		SKW05933	SKW05934					
SKW05934	West Slope Cutting (+42.5mPD to +35mPD)	32	100	02/06/11 A	03/07/11 A	02/06/11 A	03/07/11 A		SKW059331	SKW059341					
SKW059341	Revised Profile at West Slope (+20 to +4.8mPD)	1	100	04/07/11 A	04/07/11 A	04/07/11 A	04/07/11 A		SKW059322, SKW05934	SKW05935					
SKW05935	West Slope Cutting (+35mPD to +27.5mPD)	83	100	08/07/11 A	28/09/11 A	08/07/11 A	28/09/11 A		SKW059341	SKW05936					
SKW05936	West Slope Cutting (+27.5mPD to +20mPD)	61	100	29/09/11 A	28/11/11 A	29/09/11 A	28/11/11 A		SKW05935	SKW05937					
SKW05937	West Slope Cutting (+20mPD to +12.5mPD)	39	100	29/11/11 A	06/01/12 A	29/11/11 A	06/01/12 A		SKW05936	SKW05938					
SKW05938	West Slope Cutting (+12.5mPD to +4.8mPD)	90	100	07/01/12 A	27/03/12 A	07/01/12 A	27/03/12 A		SKW05937	KD0060, SKW1261, SKW1311, SKW1371					
SKW05941	Slope Stormwater Drainage	300	100	28/03/12 A	25/05/12 A	28/03/12 A	25/05/12 A		KD0060	SKW05942					
SKW059411	East Slope Cutting (+50mPD to +42.5mPD)	72	100	04/03/11 A	14/05/11 A	04/03/11 A	14/05/11 A		SKW059321	SKW059412					
SKW059412	East Slope Cutting (+42.5mPD to +35mPD)	82	100	15/05/11 A	04/08/11 A	15/05/11 A	04/08/11 A		SKW059411	SKW059413					
SKW059413	East Slope Cutting (+35mPD to +27.5mPD)	55	100	05/08/11 A	28/09/11 A	05/08/11 A	28/09/11 A		SKW059412	SKW059414					
SKW059414	East Slope Cutting (+27.5mPD to +20mPD)	61	100	29/09/11 A	28/11/11 A	29/09/11 A	28/11/11 A		SKW059413	SKW059415					
SKW059415	East Slope Cutting (+20mPD to +12.5mPD)	39	100	29/11/11 A	06/01/12 A	29/11/11 A	06/01/12 A		SKW059414	SKW059416					
SKW059416	East Slope Cutting (+12.5mPD to +4.8mPD)	81	100	07/01/12 A	27/03/12 A	07/01/12 A	27/03/12 A		SKW059415	KD0060, SKW1311, SKW1371					
SKW05942	Slope Miscellaneous Works	61	100	26/05/12 A	31/07/12 A	26/05/12 A	31/07/12 A		SKW05941	SKW05943, SKW0595					
SKW05943	Buttress & surface Protection (SI No. 31)	60	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW05942	SKW05944					
SKW05944	Slope Treatment (SI. No. 36)	60	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW05943	SKW05945					
SKW05945	Rock Slope Treatment (SI. No. 68)	60	100	01/08/12 A	30/09/12 A	01/08/12 A	30/09/12 A		SKW05944	SKW05946					
SKW05946	Rock Slope Treatment (SI. No. 98)	60	100	10/09/12 A	28/02/13 A	10/09/12 A	28/02/13 A		SKW05945	SKW05947					
SKW05947	Rock Slope Treatment (SI. No. 115)	60	100	01/11/12 A	28/02/13 A	01/11/12 A	28/02/13 A		SKW05946	KD0135					
SKW05948	Soil Nailing Works (VO. No. 52)	300	100	10/02/12 A	28/02/13 A	10/02/12 A	28/02/13 A			SKW05963					
SKW0595	Rock Meshing	60	0	06/02/14	06/04/14	07/08/15	05/10/15	547d	SKW05942, SKW05972	KD0165					
SKW05963	Determine Alignment & Foundation Design of RFB	120	100	10/02/12 A	08/06/12 A	10/02/12 A	08/06/12 A		SKW05948	SKW059631, SKW05964, SKW05965					
SKW059631	GEO Approval of Foundation Design	70	100	09/06/12 A	31/07/12 A	09/06/12 A	31/07/12 A		SKW05963	SKW05968					
SKW05964	Fabrication & Shipping of RFB Material	180	100	09/06/12 A	30/11/12 A	09/06/12 A	30/11/12 A		SKW05963	SKW05972					
SKW05965	Site clearance & Fomation of access	62	100	09/06/12 A	31/07/12 A	09/06/12 A	31/07/12 A		SKW05963	SKW05967					
SKW05967	Plant mobilization	14	100	02/01/13 A	15/01/13 A	02/01/13 A	15/01/13 A		SKW05965	SKW05968					
SKW05968	Construction of anchors & pull out test	180	70	16/01/13 A	22/06/13	16/01/13 A	21/12/14	547d	SKW059631, SKW05967	SKW05969					
SKW05969	Construction of Foundation	120	60	11/07/13 A	09/08/13	11/07/13 A	07/02/15	547d	SKW05968	SKW05970					
SKW05970	Proof Load Test	60	0	10/08/13	08/10/13	08/02/15	08/04/15	547d	SKW05969	SKW05971					
SKW05971	Transportation of Material (To the slope crest)	30	0	09/10/13	07/11/13	09/04/15	08/05/15	547d	SKW05970	SKW05972					
SKW05972	Installation of Flexible barrier	90	0	08/11/13	05/02/14	09/05/15	06/08/15	547d	SKW05964, SKW05971	KD0165, SKW0595					
Section W 5 - P.S. No. 1 in Portion D															
Civil & Geotechnical Works															
SKW0651	Site Clearance	7	100	17/05/10 A	23/05/10 A	17/05/10 A	23/05/10 A		KD0020	SKW0652					
SKW0652	Initial Survey	7	100	24/05/10 A	30/05/10 A	24/05/10 A	30/05/10 A		SKW0651	SKW0661, SKW0681					

Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	7A
© Primavera Systems, Inc.	

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ▲ Progress point
- ▲ Critical point
- ▲ Summary point
- ▲ Start milestone point
- ▲ Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013				
											APR	MAY	JUN	JUL	
SKW0661	Transplantation for uncommon vegetation	30	100	31/05/10 A	29/06/10 A	31/05/10 A	29/06/10 A		SKW0652	SKW0681					
SKW0681	Excavate to lower the working platform to +3mPD	49	100	30/06/10 A	17/08/10 A	30/06/10 A	17/08/10 A		SKW0260, SKW0265, SKW0652,	SKW0691					
SKW0691	ELS to +2.2mPD	40	100	18/08/10 A	26/09/10 A	18/08/10 A	26/09/10 A		SKW0681	SKW0721					
SKW0721	Excavate to formation	270	100	17/09/10 A	13/06/11 A	17/09/10 A	13/06/11 A		SKW0691	SKW0741					
SKW0722	Construction of Manholes (VO. No. 21A)	107	20	28/10/13 A	22/12/13	28/10/13 A	08/07/14	198d	E&M11800	E&M3360					
Structural Works															
SKW0741	RC Works for Structure	240	100	14/06/11 A	08/02/12 A	14/06/11 A	08/02/12 A		SKW0721	KD0070, SKW0841					
SKW0841	ABWF works	60	100	09/02/12 A	08/04/12 A	09/02/12 A	08/04/12 A		SKW0741	E&M1101, E&M1102, E&M1103, E&M1104,					
SKW0861	300mm U-channel & 675mm Step Channel	30	0	28/09/13	27/10/13	06/09/15	05/10/15	708d	E&M11800, SKW0841	KD0165					
E&M Works (PS1)															
Submission & Delivery															
E&M1001	Submission of Pumps	198	100	17/05/10 A	24/02/11 A	17/05/10 A	24/02/11 A		KD0020	E&M1011					
E&M1002	Submission of Gen-Set	198	100	17/05/10 A	24/02/11 A	17/05/10 A	24/02/11 A			E&M1012					
E&M1003	Submission of DeO System	198	100	17/05/10 A	16/07/13 A	17/05/10 A	16/07/13 A			E&M1013					
E&M1004	Submission of LV SB & MCC	180	100	17/05/10 A	09/01/12 A	17/05/10 A	09/01/12 A			E&M1014					
E&M1005	Submission of Instrumentation	243	100	17/05/10 A	12/03/12 A	17/05/10 A	12/03/12 A			E&M1015					
E&M1006	Submission of FS System	243	100	17/05/10 A	30/09/12 A	17/05/10 A	30/09/12 A			E&M1016					
E&M1007	Submission of BS System	243	97	17/05/10 A	07/05/13	17/05/10 A	06/12/13	213d		E&M1017					
E&M1011	Delivery of Pumps	150	100	24/02/11 A	21/07/11 A	24/02/11 A	21/07/11 A		E&M1001	E&M1101					
E&M1012	Delivery of Gen-Set	150	100	24/02/11 A	23/09/11 A	24/02/11 A	23/09/11 A		E&M1002	E&M1102					
E&M1013	Delivery of DeO System	150	100	11/07/11 A	28/10/11 A	11/07/11 A	28/10/11 A		E&M1003	E&M1103					
E&M1014	Delivery of LV SB & MCC	150	100	01/06/12 A	31/07/12 A	01/06/12 A	31/07/12 A		E&M1004	E&M1104					
E&M1015	Delivery of Instrumentation	90	100	01/11/11 A	03/11/11 A	01/11/11 A	03/11/11 A		E&M1005	E&M1105					
E&M1016	Delivery of FS Equipment	107	80	01/12/11 A	21/05/13	01/12/11 A	05/12/13	198d	E&M1006	E&M1106					
E&M1017	Delivery of BS Equipment	107	80	15/11/11 A	28/05/13	15/11/11 A	27/12/13	213d	E&M1007	E&M1107					
Installation, T&C															
E&M1101	Install Pumps	55	90	02/10/12 A	05/05/13	02/10/12 A	04/01/14	245d	E&M1011, SKW0841	E&M1110, E&M1140					
E&M1102	Install Gen Set	55	100	02/10/12 A	05/05/13 A	02/10/12 A	05/05/13 A		E&M1012, SKW0841	E&M1110, E&M1140					
E&M1103	Install DeO System	55	90	03/12/12 A	05/05/13	03/12/12 A	04/01/14	245d	E&M1013, SKW0841	E&M1110, E&M1140					
E&M1104	Install LV SB & MCC	55	100	02/01/13 A	26/03/13 A	02/01/13 A	26/03/13 A		E&M1014, SKW0841	E&M1140					
E&M1105	Install Instrumentation	55	40	01/11/12 A	01/06/13	01/11/12 A	04/01/14	217d	E&M1015, SKW0841	E&M1140					
E&M1106	Install FS Equipment	55	45	02/10/12 A	20/06/13	02/10/12 A	04/01/14	198d	E&M1016, SKW0841	E&M1130, E&M1140					
E&M1107	Install BS Equipment	55	85	02/10/12 A	05/06/13	02/10/12 A	04/01/14	213d	E&M1017, SKW0841	E&M1110, E&M1140					
E&M1110	Install Valves, Pipes & Fittings	46	100	02/01/13 A	27/03/13 A	02/01/13 A	27/03/13 A		E&M1101, E&M1102, E&M1103,	E&M1120					
E&M1120	Hydraulic Test of Pipeworks	7	50	09/05/13 A	09/06/13	09/05/13 A	13/02/14	249d	E&M1110	E&M11800					
E&M1130	Form 501 Submission to FSD	28	0	20/06/13	18/07/13	16/01/14	13/02/14	210d	E&M1106	E&M11800					
E&M1140	Cabling Works	43	80	21/05/13 A	29/06/13	21/05/13 A	13/01/14	198d	E&M1101, E&M1102, E&M1103,	E&M1150					
E&M1150	Insulation Tests of Cables and Cable Termination	7	80	25/06/13 A	30/06/13	25/06/13 A	14/01/14	198d	E&M1140	E&M1160					
E&M1160	Energization	3	20	01/07/13 A	02/07/13	01/07/13 A	17/01/14	198d	E&M1150	E&M1170					
E&M1170	Functional and Performance Tests of Equipment	30	10	02/01/13 A	29/07/13	02/01/13 A	13/02/14	198d	E&M1160	E&M11800					
E&M11800	Commissioning Test	60	0	30/07/13	27/09/13	13/02/14	14/04/14	198d	E&M0350, E&M1120, E&M1130,	SKW0722, SKW0861					
Section W 6 - Sewer and PS No.2 in Portions E&H															
Civil & Geotechnical Works															
SKW0881	Site Clearance	7	100	17/05/10 A	23/05/10 A	17/05/10 A	23/05/10 A		KD0020	SKW0891					
SKW0891	Plant mobilization	7	100	17/05/10 A	23/05/10 A	17/05/10 A	23/05/10 A		SKW0881	SKW0892					
SKW0892	Initial Survey	30	100	24/05/10 A	22/06/10 A	24/05/10 A	22/06/10 A		SKW0891	SKW0901					
SKW0901	Tree Transplantation	90	100	23/06/10 A	20/09/10 A	23/06/10 A	20/09/10 A		SKW0892	SKW0921					
SKW0921	Cut Slope & U-Channel	14	100	21/09/10 A	04/10/10 A	21/09/10 A	04/10/10 A		SKW0260, SKW0265, SKW0901	SKW0931, SKW0951					
SKW0931	Hoarding & Fencing	14	100	05/10/10 A	18/10/10 A	05/10/10 A	18/10/10 A		SKW0921	SKW0950, SKW0951					
SKW0950	Removal of Rock Boulders before ELS	66	100	19/10/10 A	23/12/10 A	19/10/10 A	23/12/10 A		SKW0931	SKW0951					
SKW0951	ELS & Excavate to formation	169	100	24/12/10 A	10/06/11 A	24/12/10 A	10/06/11 A		SKW0921, SKW0931, SKW0950	SKW0971					
SKW0961	Mass Conc. Retaining Wall	90	80	16/01/13 A	17/05/13	16/01/13 A	09/02/13	-97d	SKW1081	KD0155					
SKW1491	LCS (ChA0+45 to 1+75) VO.7	90	100	24/03/12 A	21/06/12 A	24/03/12 A	21/06/12 A		PRE0100, SKW1021	SKW15111					
SKW15111	Twin DN150 DI Rising Main (ChA1+75 - ChA5+79)	180	100	22/06/12 A	30/11/12 A	22/06/12 A	30/11/12 A		SKW1491	SKW1531					
SKW15112	Twin DN150 DI Rising Main (ChA0+00 - ChA0+45)	30	80	01/02/13 A	05/05/13	01/02/13 A	08/07/14	429d	SKW1581	E&M3360					

Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	8A
© Primavera Systems, Inc.	

	Early bar
	Progress bar
	Critical bar
	Summary bar
	Progress point
	Critical point
	Summary point
	Start milestone point
	Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013								
											APR	MAY	JUN	JUL					
SKW1531	Extent village sewers S163.1 & S164.1	34	100	30/11/12 A	10/01/13 A	30/11/12 A	10/01/13 A		SKW15111	SKW1581									
SKW1581	Construct Manhole no. S163 & S164	34	100	11/01/13 A	28/02/13 A	11/01/13 A	28/02/13 A		SKW1531	KD0135, SKW15112	63 & S164								
Structural Works																			
SKW0971	Structural Works (Phase 1)	245	100	11/06/11 A	10/02/12 A	11/06/11 A	10/02/12 A		SKW0951	KD0080, SKW1021									
SKW1021	Structural Works (Phase 2)	42	100	11/02/12 A	23/03/12 A	11/02/12 A	23/03/12 A		SKW0971	SKW1061, SKW1081, SKW1491									
SKW1061	ABWF Works	90	100	24/03/12 A	21/06/12 A	24/03/12 A	21/06/12 A		SKW1021	E&M2101, E&M2102, E&M2103, E&M2104,									
SKW1081	375mm U-channel/catchpits/outfall	30	100	22/06/12 A	31/01/13 A	22/06/12 A	31/01/13 A		SKW1021, SKW1061	KD0155, SKW0961									
E&M Works (PS2)																			
Submission & Delivery																			
E&M2001	Submission of Pumps	198	100	17/05/10 A	24/02/11 A	17/05/10 A	24/02/11 A		KD0020	E&M2011									
E&M2002	Submission of Gen-Set	198	100	17/05/10 A	24/02/11 A	17/05/10 A	24/02/11 A			E&M2012									
E&M2003	Submission of DeO System	198	100	17/05/10 A	11/07/11 A	17/05/10 A	11/07/11 A			E&M2013									
E&M2004	Submission of LV SB & MCC	271	100	17/05/10 A	30/06/12 A	17/05/10 A	30/06/12 A			E&M2014									
E&M2005	Submission of Instrumentation	243	100	17/05/10 A	30/06/12 A	17/05/10 A	30/06/12 A			E&M2015									
E&M2006	Submission of FS System	243	97	17/05/10 A	07/05/13	17/05/10 A	04/09/12	-245d		E&M2016									
E&M2007	Submission of BS System	243	97	17/05/10 A	07/05/13	17/05/10 A	26/09/12	-223d		E&M2017									
E&M2011	Delivery of Pumps	150	100	24/02/11 A	21/07/11 A	24/02/11 A	21/07/11 A		E&M2001	E&M2101									
E&M2012	Delivery of Gen-Set	150	100	24/02/11 A	23/09/11 A	24/02/11 A	23/09/11 A		E&M2002	E&M2102									
E&M2013	Delivery of DeO System	150	100	11/07/11 A	28/10/11 A	11/07/11 A	28/10/11 A		E&M2003	E&M2103									
E&M2014	Delivery of LV SB & MCC	150	100	29/02/12 A	31/07/12 A	29/02/12 A	31/07/12 A		E&M2004	E&M2104									
E&M2015	Delivery of Instrumentation	90	100	21/06/11 A	03/11/11 A	21/06/11 A	03/11/11 A		E&M2005	E&M2105									
E&M2016	Delivery of FS Equipment	107	80	01/12/11 A	28/05/13	01/12/11 A	25/09/12	-245d	E&M2006	E&M0350, E&M2106									
E&M2017	Delivery of BS Equipment	107	80	15/01/11 A	28/05/13	15/01/11 A	17/10/12	-223d	E&M2007	E&M2107									
Installation, T&C																			
E&M2101	Install Pumps	55	80	02/10/12 A	10/05/13	02/10/12 A	12/01/13	-118d	E&M2011, SKW1061	E&M2110									
E&M2102	Install Gen Set	55	100	01/09/12 A	05/05/13 A	01/09/12 A	05/05/13 A		E&M2012, SKW1061	E&M2110									
E&M2103	Install DeO System	55	90	03/12/12 A	05/05/13	03/12/12 A	12/01/13	-113d	E&M2013, SKW1061	E&M2110									
E&M2104	Install LV SB & MCC	55	100	02/01/13 A	31/01/13 A	02/01/13 A	31/01/13 A		E&M2014, SKW1061	E&M2140									
E&M2105	Install Instrumentation	55	0	30/04/13	23/06/13	01/09/12	25/10/12	-241d	E&M2015, SKW1061	E&M2140									
E&M2106	Install FS Equipment	55	45	02/10/12 A	27/06/13	02/10/12 A	25/10/12	-245d	E&M2016, SKW1061	E&M2140									
E&M2107	Install BS Equipment	55	85	01/09/12 A	05/06/13	01/09/12 A	25/10/12	-223d	E&M2017, SKW1061	E&M2110, E&M2140									
E&M2110	Install Valves, Pipes & Fittings	46	100	02/01/13 A	31/01/13 A	02/01/13 A	31/01/13 A		E&M2101, E&M2102, E&M2103,	E&M2120									
E&M2120	Hydraulic Test of Pipeworks	7	100	02/01/13 A	31/01/13 A	02/01/13 A	31/01/13 A		E&M2110	E&M2130									
E&M2130	Form 501 Submission to FSD	28	0	05/06/13	03/07/13	13/01/13	09/02/13	-144d	E&M2120	KD0155									
E&M2140	Cabling Works	43	60	01/02/13 A	15/07/13	01/02/13 A	12/11/12	-245d	E&M2104, E&M2105, E&M2106,	E&M2150									
E&M2150	Insulation Tests of Cables and Cable Termination	7	60	01/02/13 A	17/07/13	01/02/13 A	14/11/12	-245d	E&M2140	E&M2160									
E&M2160	Energization	3	100	01/02/13 A	25/03/13 A	01/02/13 A	25/03/13 A		E&M2150	E&M2170									
E&M2170	Functional and Performance Tests of Equipment	30	10	15/01/13 A	13/08/13	15/01/13 A	11/12/12	-245d	E&M2160	E&M2180									
E&M2180	Commissioning Test	60	0	13/08/13	12/10/13	12/12/12	09/02/13	-245d	E&M0350, E&M2170	KD0155									
Section W 7 - SKW STW ,Sewer and Submarine Outfall																			
Submarine Outfall																			
SKW1130	Approval of IHS Consultant	180	100	17/05/10 A	27/08/10 A	17/05/10 A	27/08/10 A			SKW1131									
SKW1131	Hydrographical Survey (SKW)	300	100	01/02/11 A	28/02/11 A	01/02/11 A	28/02/11 A		KD0020, SKW1130	SKW1231									
SKW1141	Baseline Monitoring (Water)	213	100	27/07/10 A	31/12/10 A	27/07/10 A	31/12/10 A		SKW0260, SKW0265	SKW1151									
SKW1151	Set up Temporary Working Platform	90	100	15/06/11 A	30/09/11 A	15/06/11 A	30/09/11 A		PRE0090, SKW1141	SKW1171									
SKW1171	ELS for HDD Set-up (SKW)	90	100	01/09/11 A	30/09/11 A	01/09/11 A	30/09/11 A		SKW1151	SKW1181									
SKW1181	Mobilization of HDD plant & equipment to SKW	8	100	06/01/12 A	07/01/12 A	06/01/12 A	07/01/12 A		SKW1171, YSW0360	SKW1191									
SKW1191	Setting up at drillhole location	7	100	09/01/12 A	14/01/12 A	09/01/12 A	14/01/12 A		SKW1181	SKW1201									
SKW1201	Drill pilot hole and reaming hole - NS280 - 750m	33	100	16/01/12 A	16/02/12 A	16/01/12 A	16/02/12 A		SKW1191	SKW1211									
SKW1211	Receiving Pit for HDD (SKW)	13	100	16/01/12 A	29/02/12 A	16/01/12 A	29/02/12 A		SKW1201	SKW1221									
SKW1221	Installation of NS280 HDPE 450mm dia. pipe	61	100	31/03/12 A	30/04/12 A	31/03/12 A	30/04/12 A		SKW1211	KD0090, SKW1231, SKW1441									
SKW1231	Removal of Receiving Platform	50	100	01/05/12 A	19/06/12 A	01/05/12 A	19/06/12 A		SKW1131, SKW1221	SKW1241									
SKW1241	Dredging of MD for Diffuser (PS CL 1.122(3))	16	100	20/06/12 A	05/07/12 A	20/06/12 A	05/07/12 A		SKW1231	E&M3359, SKW1251									
SKW1251	Diffuser Construction	77	100	01/09/12 A	16/11/12 A	01/09/12 A	16/11/12 A		SKW1241	SKW1431									
SKW1431	Removal of silt curtain	1	100	17/11/12 A	17/11/12 A	17/11/12 A	17/11/12 A		SKW1251	KD0090, SKW1440, YSW0365									
SKW1440	Sewer of Outfall Chamber to connection pit VO37A	90	60	31/12/12 A	04/06/13	31/12/12 A	07/03/14	276d	SKW1431	SKW1441									
Start date	05/05/10											Date	30/04/13	Revision	Revision 0	Checked	RH	Approved	VC
Finish date	13/01/17																		
Data date	30/04/13																		
Run date	20/05/13																		
Page number	9A																		
c Primavera Systems, Inc.																			

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ▲ Progress point
- ▲ Critical point
- ▲ Summary point
- ▲ Start milestone point
- ▲ Finish milestone point

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013			
											APR	MAY	JUN	JUL
SKW1441	Sewer of Connection Pit to Outfall VO45	177	50	05/06/13 A	01/09/13	05/06/13 A	03/06/14	276d	SKW1221, SKW1440	E&M3359, KD0090				
SKW STW														
Submission & Delivery (E&M)														
E&M3010	Delivery of MBR M.M. - 1st shipment for Temp STP	150	100	24/02/11 A	17/10/11 A	24/02/11 A	17/10/11 A		E&M0160	E&M3170				
E&M3030	Delivery of Grit Removal Equipment	180	100	10/10/11 A	29/12/11 A	10/10/11 A	29/12/11 A		E&M0150	E&M3190				
E&M3060	Delivery of Fine Screens	136	100	12/09/11 A	30/11/11 A	12/09/11 A	30/11/11 A		E&M0120	E&M3210				
E&M3070	Delivery of Pumps	136	100	23/06/11 A	05/09/11 A	23/06/11 A	05/09/11 A		E&M0130	E&M3220				
E&M3080	Delivery of Submersible Mixers	180	100	26/07/11 A	17/11/11 A	26/07/11 A	17/11/11 A		E&M0140	E&M3230				
E&M3090	Delivery of Sludge Dewatering Equipment	210	50	01/09/11 A	12/08/13	01/09/11 A	11/01/14	152d	E&M0170	E&M3240				
E&M3100	Delivery of Valves, Pipes & Fittings	180	50	30/08/11 A	02/08/13	30/08/11 A	19/11/13	110d	E&M0180	E&M3250				
E&M3110	Delivery of Penstocks	180	100	12/08/11 A	24/12/11 A	12/08/11 A	24/12/11 A		E&M0190	E&M3260				
E&M3130	Delivery of instruments	180	100	21/06/11 A	03/11/11 A	21/06/11 A	03/11/11 A		E&M0200	E&M3270				
E&M3140	Delivery of MCC LVSB	180	0	01/05/13	28/10/13	07/04/13	03/10/13	-25d	E&M0210	E&M3261				
E&M3150	Delivery of BS Equipment	180	8	03/07/12 A	17/11/13	03/07/12 A	04/12/13	18d	E&M0220	E&M3291				
E&M3160	Delivery of FS Equipment	180	5	30/06/12 A	04/12/13	30/06/12 A	23/12/13	20d	E&M0230	E&M0340, E&M3300				
Construction of Grid A-G														
SKW1261	Excavate for SKW STW Structure (Grid A -G)	164	100	28/03/12 A	31/08/12 A	28/03/12 A	31/08/12 A		SKW04885, SKW05938	SKW1271, SKW1371				
SKW1271	55 M3 Fire Sprinkle Water Tank (FL +0.9 mPD)	36	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW1261	SKW1281				
SKW1281	Ground Floor Slab (Grid A-G)	46	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW1271	SKW1291				
SKW1291	Columns & Walls to 1/F & 1/F Slab (Grid A-G)	50	100	03/07/12 A	31/07/12 A	03/07/12 A	31/07/12 A		SKW1281	KD0090, SKW1301				
SKW1301	Columns & Walls to R/F & R/F Slab (Grid A-G)	50	100	01/09/12 A	31/01/13 A	01/09/12 A	31/01/13 A		SKW1291	E&M3261, E&M3291, E&M3311, SKW1411				
SKW1411	ABWF Works	105	10	01/02/13 A	02/08/13	01/02/13 A	19/06/13	-44d	SKW1301	E&M3261, E&M3291, E&M3311, SKW1551				
Construction of Grid G-N														
SKW1311	Excavate for SKW STW Structure (Grid G-N)	90	100	28/03/12 A	25/06/12 A	28/03/12 A	25/06/12 A		SKW05938, SKW059416	SKW1321, SKW1371				
SKW1321	Equalization Tank no.1 & 2 with base slabs (-2.1	42	100	26/06/12 A	30/09/12 A	26/06/12 A	30/09/12 A		SKW1311	SKW1331				
SKW1331	Columns & Walls from B/S to G/F Slab (Grid G-N)	35	100	01/09/12 A	30/09/12 A	01/09/12 A	30/09/12 A		SKW1321	SKW1341				
SKW1341	Ground Floor Slab (Grid G-N)	35	100	01/09/12 A	17/12/12 A	01/09/12 A	17/12/12 A		SKW1331	SKW1351				
SKW1351	Columns & Walls to 1/F & 1/F Slab (Grid G-N)	28	100	01/11/12 A	15/01/13 A	01/11/12 A	15/01/13 A		SKW1341	SKW1361				
SKW1361	Columns & Walls to R/F & R/F Slab (Grid G-N)	35	70	01/11/12 A	10/05/13	01/11/12 A	01/02/13	-98d	SKW1351	SKW1451				
SKW1451	ABWF Works	54	0	10/05/13	03/07/13	01/02/13	27/03/13	-98d	SKW1361	E&M3170, E&M3190, E&M3210, E&M3291, E&M3300, SKW1391, SKW1551				
Construction of Grid N-T														
SKW1371	Excavate for SKW STW Structure (Grid N-T)	97	100	03/07/12 A	25/01/13 A	03/07/12 A	25/01/13 A		SKW05938, SKW059416, SKW1261,	SKW1381				
SKW1381	Ground Floor Slabs include MBR Tank (Grid N-T)	58	100	02/10/12 A	31/01/13 A	02/10/12 A	31/01/13 A		SKW1371	SKW1391				
SKW1391	Columns & Walls to 1/F & 1/F Slab (Grid N-T)	35	100	31/05/13 A	05/07/13 A	31/05/13 A	05/07/13 A		SKW1381, SKW1451	SKW1401				
SKW1401	Columns & Walls to R/F & R/F Slab (Grid N-T)	35	30	03/07/13 A	27/07/13	03/07/13 A	20/04/13	-98d	SKW1391	E&M3240, SKW0491, SKW1421				
SKW1421	ABWF Works	60	0	28/07/13	25/09/13	21/04/13	19/06/13	-98d	SKW1401	E&M3240, SKW1551				
SKW1551	Drainage (SSMH1-SSMH7)	35	0	26/09/13	30/10/13	20/06/13	24/07/13	-98d	SKW1411, SKW1421, SKW1451	SKW1561				
SKW1561	Sewer (SMFH1-SMFH2, SMFH3-SMFH7)	220	0	31/10/13	07/06/14	25/07/13	01/03/14	-98d	SKW1551	SKW1571				
SKW1571	Roadwork & Drainage Channel (SKW)	220	0	08/06/14	13/01/15	02/03/14	07/10/14	-98d	SKW1561	KD0090				
SKW STW - E&M Works														
E&M3170	Install Membrane Modules in MBR Tank No. 1 to 2	100	0	03/07/13	11/10/13	07/01/14	16/04/14	188d	E&M3010, SKW1451	E&M3311				
E&M3190	Install Grit Removal Equipment	60	0	01/09/13	31/10/13	21/09/13	19/11/13	20d	E&M3030, E&M3210, SKW1451	E&M3250, E&M3320				
E&M3210	Install Fine Screens	60	0	03/07/13	01/09/13	24/05/13	22/07/13	-41d	E&M3060, SKW1451	E&M3190, E&M3220, E&M3250, E&M3260, E&M3320				
E&M3220	Install Pumps	75	0	01/09/13	15/11/13	23/07/13	05/10/13	-41d	E&M3070, E&M3210	E&M3230, E&M3250, E&M3260, E&M3320				
E&M3230	Install Submersible Mixers	45	0	15/11/13	30/12/13	06/10/13	19/11/13	-41d	E&M3080, E&M3220	E&M3250, E&M3260, E&M3311, E&M3320				
E&M3240	Install Sludge Dewatering Equipment	74	0	26/09/13	08/12/13	12/01/14	26/03/14	108d	E&M3090, SKW1401, SKW1421	E&M3320				
E&M3250	Install Valves, Pipes & Fittings	75	0	30/12/13	15/03/14	20/11/13	02/02/14	-41d	E&M3100, E&M3190, E&M3210, E&M3220, E&M3230	E&M3270, E&M3291, E&M3300, E&M3310				
E&M3260	Install Penstocks	135	0	30/12/13	14/05/14	03/12/13	16/04/14	-28d	E&M3110, E&M3210, E&M3220,	E&M3311				
E&M3261	Install SAT of MCC & LVSB	174	0	28/10/13	20/04/14	04/10/13	26/03/14	-25d	E&M3140, SKW1301, SKW1411	E&M3311, E&M3320				
E&M3270	Install instruments	60	0	15/03/14	14/05/14	16/02/14	16/04/14	-28d	E&M3130, E&M3250	E&M3311				
E&M3291	Install BS Equipment	180	0	14/01/14	13/07/14	05/12/13	02/06/14	-41d	E&M3150, E&M3250, SKW1301, SKW1411, SKW1451	E&M3331, E&M3359				










Start date	05/05/10
Finish date	13/01/17
Data date	30/04/13
Run date	20/05/13
Page number	10A
© Primavera Systems, Inc.	

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ▲ Progress point
- ▲ Critical point
- ◆ Summary point
- ◆ Start milestone point
- ◆ Finish milestone point

Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC

Activity ID	Description	Original Duration	Percent Complete	Early Start	Early Finish	Late Start	Late Finish	Total Float	Predecessors	Successors	2013				
											APR	MAY	JUN	JUL	
E&M3300	Install FS Equipment	161	0	14/01/14	24/06/14	24/12/13	02/06/14	-22d	E&M3160, E&M3250, SKW1451	E&M3331, E&M3359					
E&M3310	Hydraulic Tests of Pipeworks	90	0	15/03/14	13/06/14	06/03/14	03/06/14	-10d	E&M3250	E&M3359					
E&M3311	Cabling Works	47	0	14/05/14	30/06/14	17/04/14	02/06/14	-28d	E&M3170, E&M3230, E&M3260, E&M3261, E&M3270, SKW1301,	E&M3331, E&M3359					
E&M3320	Cabling Works for Dewatering Equipment	47	0	20/04/14	06/06/14	27/03/14	12/05/14	-25d	E&M3190, E&M3210, E&M3220, E&M3230, E&M3240, E&M3261	E&M3321					
E&M3321	Insulation Tests of Cables and Cable Termination	21	0	06/06/14	27/06/14	13/05/14	02/06/14	-25d	E&M3320	E&M3331					
E&M3331	Energization	1	0	13/07/14	14/07/14	03/06/14	03/06/14	-41d	E&M3291, E&M3300, E&M3311,	E&M3359					
E&M3359	Functional and Performance Tests of Equipment	35	0	14/07/14	18/08/14	04/06/14	08/07/14	-41d	E&M3291, E&M3300, E&M3310, E&M3311, E&M3331, SKW1241,	E&M3360					
E&M3360	T&C Period	91	0	18/08/14	17/11/14	09/07/14	07/10/14	-41d	E&M0340, E&M3359, SKW0722, SKW15112	E&M3370, KD0090					
E&M3370	Trial Operation Period	456	0	17/11/14	16/02/16	25/07/15	13/01/17	250d	E&M3360						
Rising Main															
SKW1481	Subm, Approval & Delivery of DI pipes	120	100	17/05/10 A	13/09/10 A	17/05/10 A	13/09/10 A		KD0020	SKW1501					
SKW1501	LCS (ChB0+00 - ChB1+20)	300	100	14/09/10 A	10/07/11 A	14/09/10 A	10/07/11 A		PRE0100, SKW1481	SKW1521					
SKW1521	Twin DN150 DI Rising Main (ChB0+00 - ChA4+55)	250	85	11/07/11 A	06/06/13	11/07/11 A	07/10/14	489d	SKW1501	KD0090					
Section W8 - Landscape Softworks in All Portions															
SKW1591	Tree Survey	21	100	17/05/10 A	06/06/10 A	17/05/10 A	06/06/10 A		KD0020	SKW1621					
SKW1611	Preservation & Protection of Trees	1053	99	17/05/10 A	10/05/13	17/05/10 A	03/04/13	-37d	KD0020	KD0100, SKW1631					
SKW1621	Transplantation at SKW	90	100	07/06/10 A	04/09/10 A	07/06/10 A	04/09/10 A		SKW1591	KD0100					
Section W9 - Establishment Works in All Portions															
SKW1631	Section W9 - Establishment Works	365	0	10/05/13	10/05/14	04/04/13	03/04/14	-37d	SKW1611	KD0110					


Start date	05/05/10		Early bar
Finish date	13/01/17		Progress bar
Data date	30/04/13		Critical bar
Run date	20/05/13		Summary bar
Page number	11A		Progress point
c Primavera Systems, Inc.			Critical point
			Summary point
			Start milestone point
			Finish milestone point


Leader Civil Engineering Corp. Ltd.
Contract No. DC/2009/13
Construction of Sewage Treatment Works at YSW & SKW
3-month Rolling Programme (May 2013 - July 2013)

Date	Revision	Checked	Approved
30/04/13	Revision 0	RH	VC


Appendix D

Location of Monitoring Stations (Air Quality / Construction Noise / Water Quality / Dive Surveys of Coral)

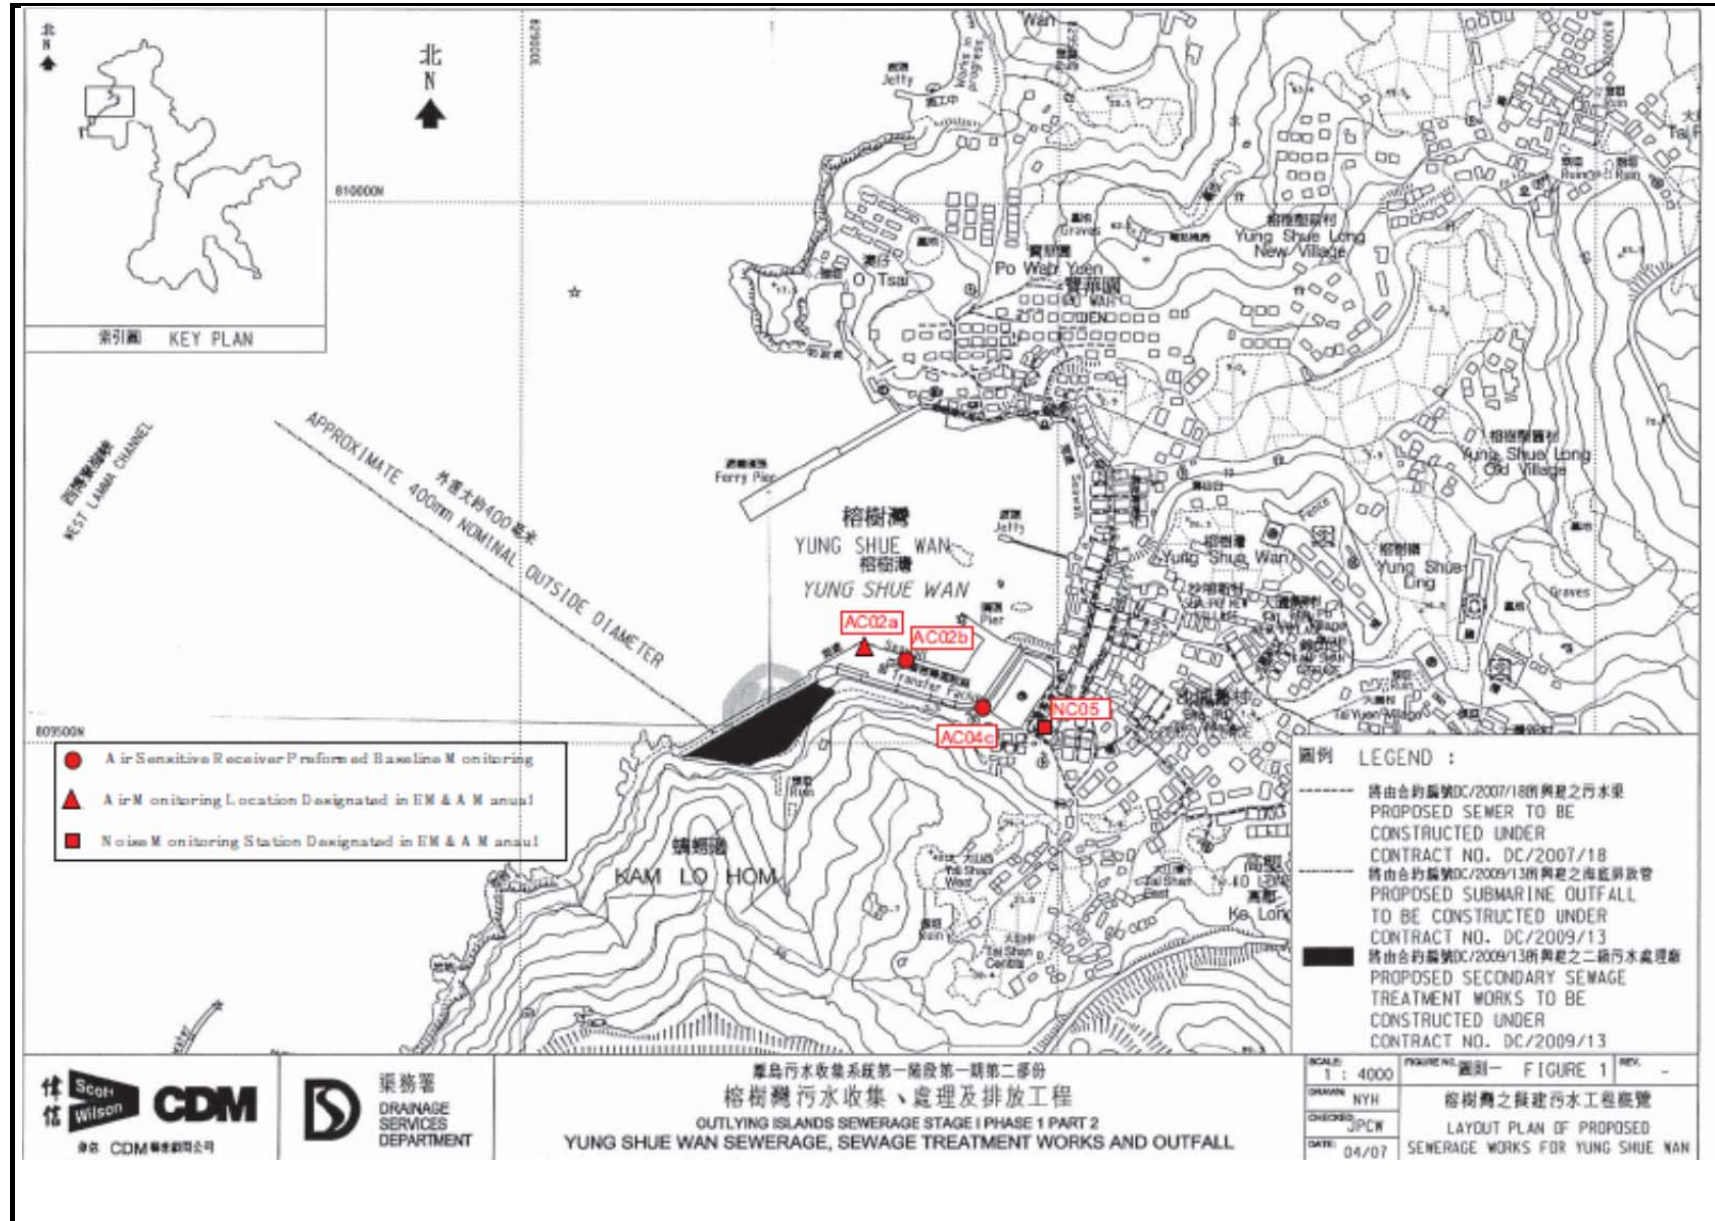


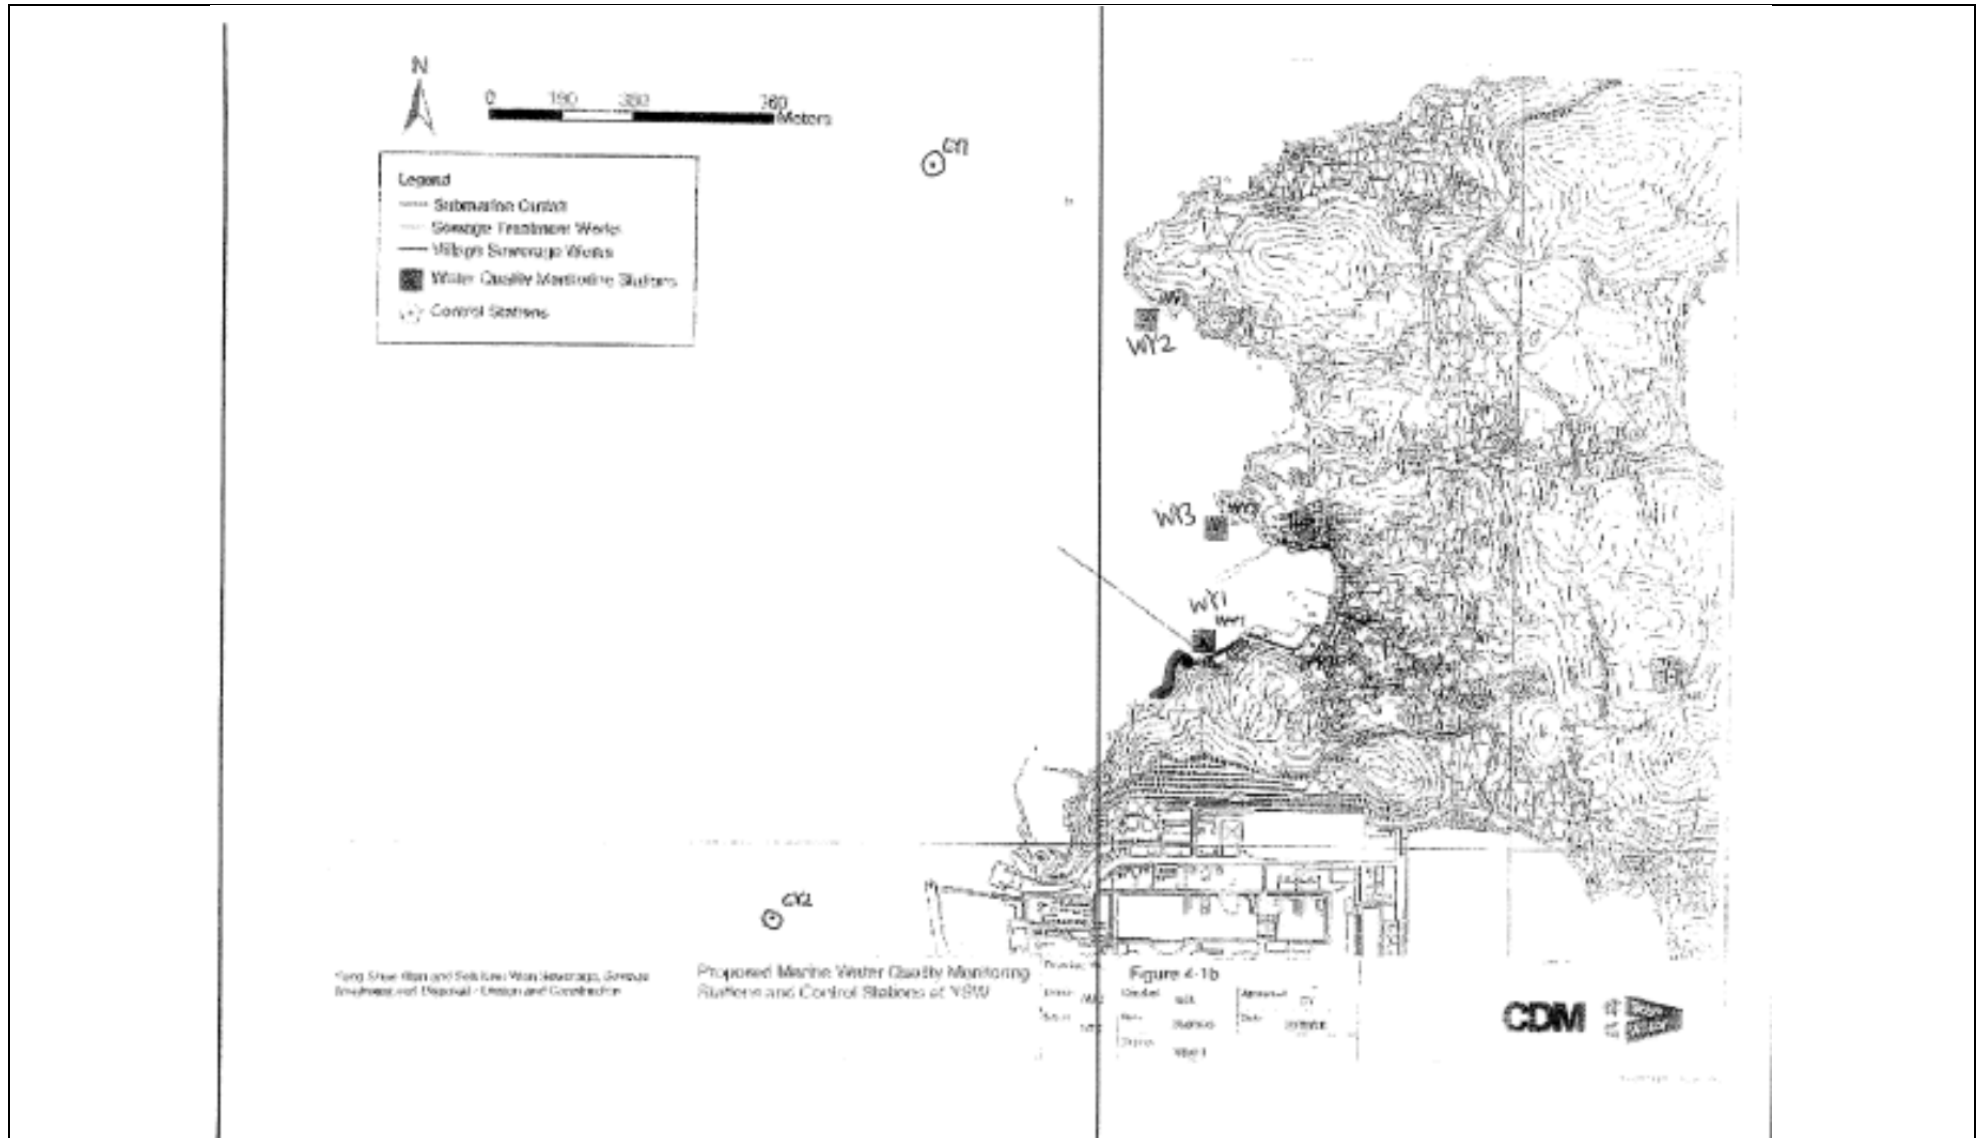

Coral Area at Yung Shue Wan Seawall

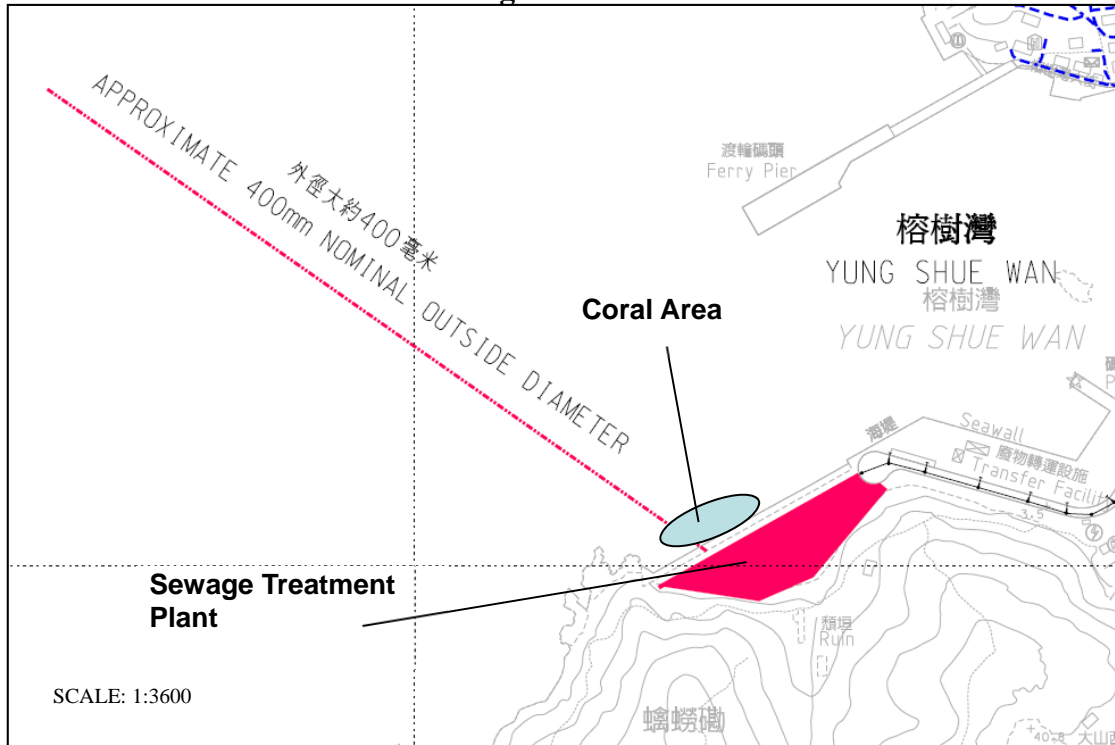

REA Transect at Yung Shue Wan Seawall

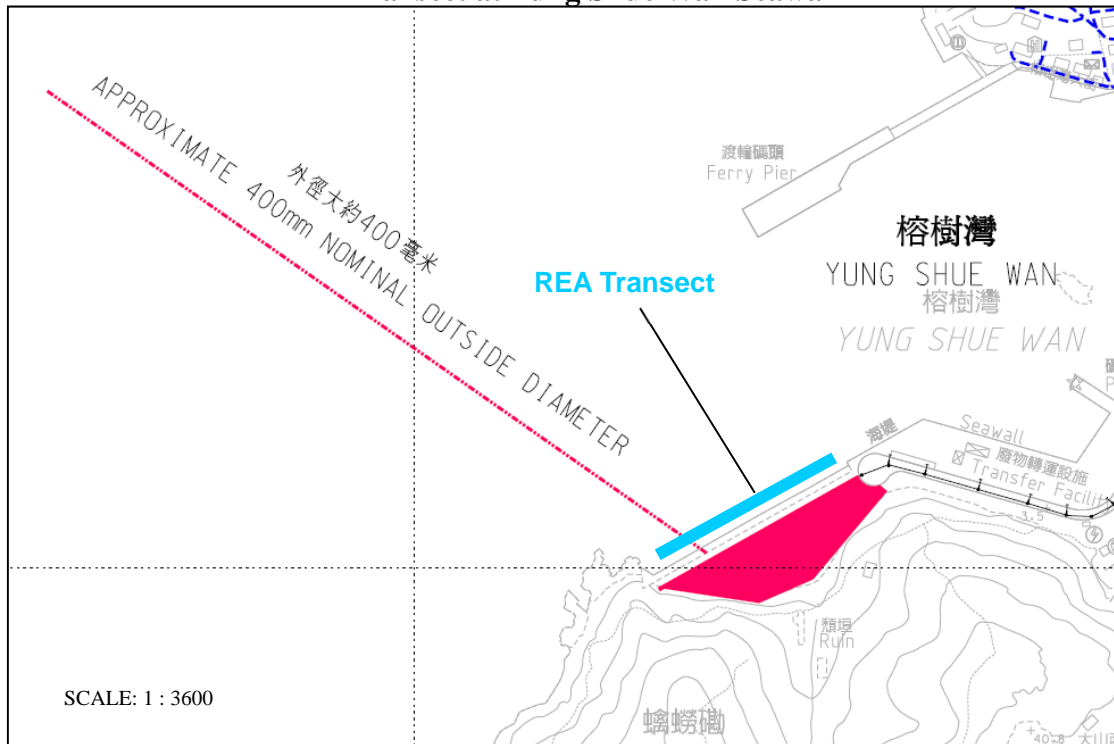

Coral Area at Sham Wan



REA Transect at Sham Wan



Appendix E

Monitoring Equipments Calibration Certificate

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : YSW RE Offices
 Location ID : AC02b

Date of Calibration: 2-Apr-13
 Next Calibration Date: 2-Jun-13
 Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa)	1014	Corrected Pressure (mm Hg)	760.5
Temperature (°C)	21.1	Temperature (K)	294

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11693
Model->	5025A	Qstd Intercept ->	-0.02568
Serial # ->	1941		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.8	5.8	11.6	1.632	59	59.80	Slope = 26.9315 Intercept = 15.6648 Corr. coeff. = 0.9979
13	4.5	4.5	9	1.439	54	54.73	
10	3.3	3.3	6.6	1.234	48	48.65	
7	2.3	2.3	4.6	1.032	42	42.57	
5	1.2	1.2	2.4	0.749	36	36.49	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

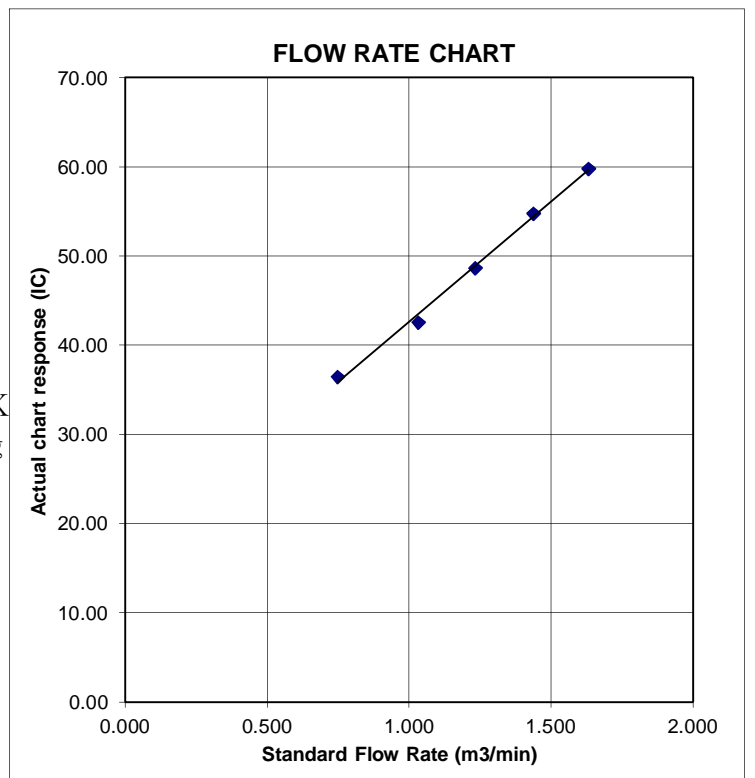

TSP SAMPLER CALIBRATION CALCULATION SPREADSHEET

Location : YSW Playground
 Location ID : AC04c

Date of Calibration: 2-Apr-13
 Next Calibration Date: 2-Jun-13
 Technician: Mr. Ben Tam

CONDITIONS

Sea Level Pressure (hPa)	1014	Corrected Pressure (mm Hg)	760.5
Temperature (°C)	21.1	Temperature (K)	294

CALIBRATION ORIFICE

Make->	TISCH	Qstd Slope ->	2.11693
Model->	5025A	Qstd Intercept ->	-0.02568
Serial # ->	1941		

CALIBRATION

Plate No.	H2O (L) (in)	H2O (R) (in)	H2O (in)	Qstd (m3/min)	I (chart)	IC corrected	LINEAR REGRESSION
18	5.3	5.3	10.6	1.561	59	59.80	Slope = 33.8766 Intercept = 6.9583 Corr. coeff. = 0.9999
13	4.1	4.1	8.2	1.374	53	53.72	
10	3	3	6	1.177	46	46.63	
7	2	2	4	0.963	39	39.53	
5	1.2	1.2	2.4	0.749	32	32.44	

Calculations :

$$Qstd = 1/m[\text{Sqrt}(H2O(Pa/Pstd)(Tstd/Ta))-b]$$


$$IC = I[\text{Sqrt}(Pa/Pstd)(Tstd/Ta)]$$

Qstd = standard flow rate
 IC = corrected chart responses
 I = actual chart response
 m = calibrator Qstd slope
 b = calibrator Qstd intercept
 Ta = actual temperature during calibration (deg K)
 Pstd = actual pressure during calibration (mm Hg)

For subsequent calculation of sampler flow:

$$1/m((I)[\text{Sqrt}(298/Tav)(Pav/760)]-b)$$

m = sampler slope
 b = sampler intercept
 I = chart response
 Tav = daily average temperature
 Pav = daily average pressure

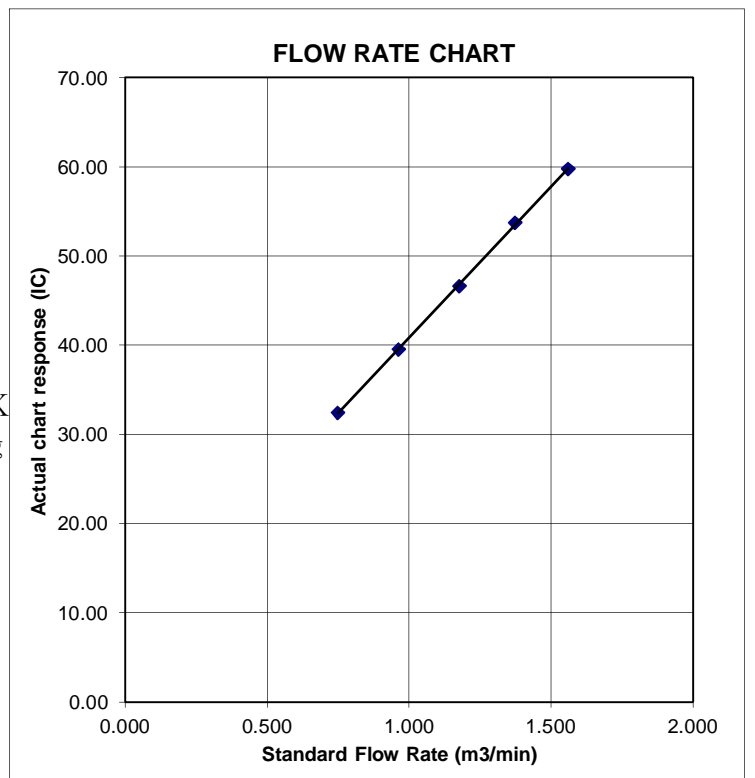

Equipment Calibration Record

Equipment Calibrated:

Type: Dust Trak Model 8520
 Manufacturer: TSI
 Serial No. 21060
 Equipment Ref: EQ021

Standard Equipment:

Standard Equipment: Higher Volume Sampler
 Location & Location ID: Block A of Government Dockyard Offices
 Equipment Ref: AM8
 Last Calibration Date: 20-Jul-12

Equipment Calibration Results:


Calibration Date: 6-Aug-12

Hour	Time	Temp °C	RH %	Dust Concentration in mg/m ³	
				(Standard Equipment)	(Calibrated Equipment)
1	9:00 ~ 10:00	29.8	84	0.052	0.056
1	10:05 ~ 11:05	30.2	84	0.057	0.066
1	11:10 ~ 12:10	30.9	84	0.044	0.046

Sensitivity Adjustment Zero Calibration (Before Calibration) 0 (mg/m³)
 Sensitivity Adjustment Zero Calibration (After Calibration) 0 (mg/m³)

Linear Regression of Y or X

Slope: 1.1155
 Correlation Coefficient 0.9931

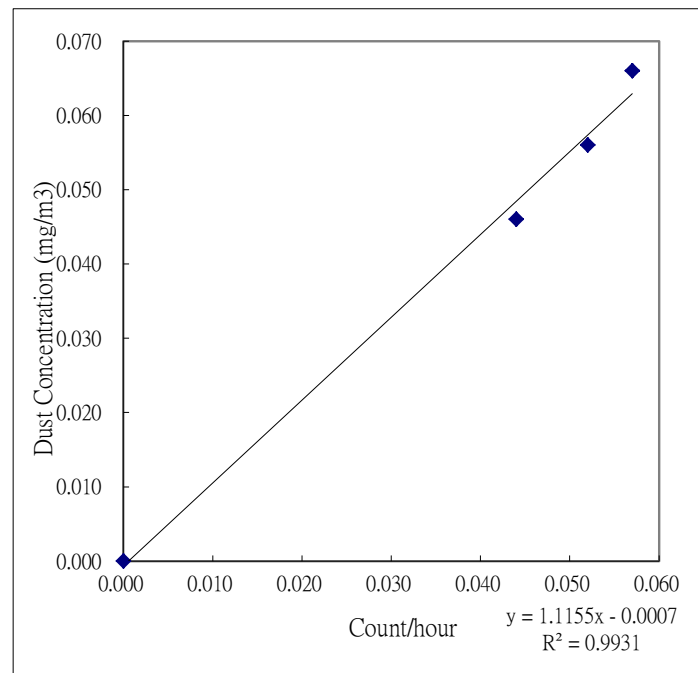

Operator : Ray Cheung

Signature : *Ray*

Date : 8/8/2012

QC Reviewer Ben Tam

Signature : *[Signature]*

Date : 8/8/2012



TISCH ENVIRONMENTAL, INC.
 145 SOUTH MIAMI AVE.
 VILLAGE OF CLEVELAND, OH 45002
 513.467.9000
 877.263.7610 TOLL FREE
 513.467.9009 FAX
 WWW.TISCH-ENV.COM

AIR POLLUTION MONITORING EQUIPMENT

ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - May 17, 2012 Rootsometer S/N 0438320 Ta (K) - 294
 Operator Tisch Orifice I.D. - 1483 Pa (mm) - 754.38

PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER	ORFICE
					DIFF Hg (mm)	DIFF H2O (in.)
1	NA	NA	1.00	1.4140	3.2	2.00
2	NA	NA	1.00	0.9960	6.4	4.00
3	NA	NA	1.00	0.8910	7.9	5.00
4	NA	NA	1.00	0.8510	8.7	5.50
5	NA	NA	1.00	0.7020	12.8	8.00

DATA TABULATION

Vstd	(x axis) Qstd	(y axis)	Va	(x axis) Qa	(y axis)
1.0018	0.7085	1.4185	0.9957	0.7042	0.8829
0.9976	1.0016	2.0061	0.9915	0.9955	1.2486
0.9955	1.1173	2.2429	0.9894	1.1105	1.3959
0.9945	1.1686	2.3524	0.9884	1.1615	1.4641
0.9890	1.4088	2.8371	0.9830	1.4003	1.7657
Qstd slope (m) = 2.02742			Qa slope (m) = 1.26953		
intercept (b) = -0.02027			intercept (b) = -0.01262		
coefficient (r) = 0.99996			coefficient (r) = 0.99996		
y axis = SQRT[H2O(Pa/760) (298/Ta)]			y axis = SQRT[H2O(Ta/Pa)]		

CALCULATIONS

$$Vstd = \text{Diff. Vol}[(Pa - \text{Diff. Hg})/760] (298/Ta)$$

$$Qstd = Vstd/Time$$

$$Va = \text{Diff Vol} [(Pa - \text{Diff Hg})/Pa]$$

$$Qa = Va/Time$$

For subsequent flow rate calculations:

$$Qstd = 1/m\{[\text{SQRT}(H2O(Pa/760) (298/Ta))]\} - b\}$$

$$Qa = 1/m\{[\text{SQRT} H2O(Ta/Pa)] - b\}$$



Certificate of Calibration 校正證書

Certificate No. : C132568
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC13-0878)

Description / 儀器名稱 : Integrating Sound Level Meter (EQ006)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 2238
Serial No. / 編號 : 2285762
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$ Relative Humidity / 相對濕度 : $(55 \pm 20)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check


DATE OF TEST / 測試日期 : 27 April 2013

TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).

The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Agilent Technologies, USA
- Fluke Everett Service Center, USA
- Rohde & Schwarz Laboratory, Germany

Tested By : 
測試 H C Chan

Certified By : 
核證 K C Lee

Date of Issue : 30 April 2013
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C132568
證書編號

1. The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours, and switched on to warm up for over 10 minutes before the commencement of the test.
2. Self-calibration using laboratory acoustic calibrator was performed before the test from 6.1.1.2 to 6.4.
3. The results presented are the mean of 3 measurements at each calibration point.
4. Test equipment :

Equipment ID	Description	Certificate No.
CL280	40 MHz Arbitrary Waveform Generator	C130019
CL281	Multifunction Acoustic Calibrator	DC110233

5. Test procedure : MA101N.

6. Results :

- 6.1 Sound Pressure Level

- 6.1.1 Reference Sound Pressure Level

- 6.1.1.1 Before Self-calibration

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
50 - 130	L _{AFF}	A	F	94.00	1	93.6

- 6.1.1.2 After Self-calibration

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L _{AFF}	A	F	94.00	1	94.0	± 0.7

- 6.1.2 Linearity

UUT Setting				Applied Value		UUT Reading (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)	
50 - 130	L _{AFF}	A	F	94.00	1	94.0 (Ref.)
				104.00		104.0
				114.00		114.0

IEC 60651 Type 1 Spec. : ± 0.4 dB per 10 dB step and ± 0.7 dB for overall different.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載按正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室所書面批准。

Certificate of Calibration

校正證書

Certificate No. : C132568
證書編號

6.2 Time Weighting

6.2.1 Continuous Signal

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq. (kHz)		
50 - 130	L _{AFP}	A	F	94.00	1	94.0	Ref.
	L _{ASP}		S			94.0	± 0.1
	L _{AIP}		I			94.1	± 0.1

6.2.2 Tone Burst Signal (2 kHz)

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Burst Duration		
30 - 110	L _{AFP}	A	F	106.0	Continuous	106.0	Ref.
	L _{AFMax}				200 ms	104.9	-1.0 ± 1.0
	L _{ASP}	S	Continuous		106.0	Ref.	
	L _{ASMax}		500 ms		101.9	-4.1 ± 1.0	

6.3 Frequency Weighting

6.3.1 A-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{AFP}	A	F	94.00	31.5 Hz	55.1	-39.4 ± 1.5
					63 Hz	67.9	-26.2 ± 1.5
					125 Hz	77.8	-16.1 ± 1.0
					250 Hz	85.3	-8.6 ± 1.0
					500 Hz	90.7	-3.2 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	95.2	+1.2 ± 1.0
					4 kHz	95.0	+1.0 ± 1.0
					8 kHz	92.9	-1.1 (+1.5 ; -3.0)
					12.5 kHz	89.8	-4.3 (+3.0 ; -6.0)

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Certificate of Calibration

校正證書

Certificate No. : C132568
證書編號

6.3.2 C-Weighting

UUT Setting				Applied Value		UUT Reading (dB)	IEC 60651 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Time Weighting	Level (dB)	Freq.		
50 - 130	L _{CFP}	C	F	94.00	31.5 Hz	91.4	-3.0 ± 1.5
					63 Hz	93.3	-0.8 ± 1.5
					125 Hz	93.8	-0.2 ± 1.0
					250 Hz	94.0	0.0 ± 1.0
					500 Hz	94.0	0.0 ± 1.0
					1 kHz	94.0	Ref.
					2 kHz	93.8	-0.2 ± 1.0
					4 kHz	93.2	-0.8 ± 1.0
					8 kHz	90.9	-3.0 (+1.5 ; -3.0)
					12.5 kHz	87.8	-6.2 (+3.0 ; -6.0)

6.4 Time Averaging

UUT Setting				Applied Value					UUT Reading (dB)	IEC 60804 Type 1 Spec. (dB)
Range (dB)	Parameter	Frequency Weighting	Integrating Time	Frequency (kHz)	Burst Duration (ms)	Burst Duty Factor	Burst Level (dB)	Equivalent Level (dB)		
30 - 110	L _{Aeq}	A	10 sec.	4	1	1/10	110.0	100	100.0	± 0.5
								90	89.8	± 0.5
								80	79.4	± 1.0
								70	69.2	± 1.0

Remarks : - Mfr's Spec. : IEC 60651 Type 1 & IEC 60804 Type 1

- Uncertainties of Applied Value :

94 dB : 31.5 Hz - 125 Hz	: ± 0.35 dB
250 Hz - 500 Hz	: ± 0.30 dB
1 kHz	: ± 0.20 dB
2 kHz - 4 kHz	: ± 0.35 dB
8 kHz	: ± 0.45 dB
12.5 kHz	: ± 0.70 dB
104 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)
114 dB : 1 kHz	: ± 0.10 dB (Ref. 94 dB)
Burst equivalent level	: ± 0.2 dB (Ref. 110 dB continuous sound level)

- The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書請先獲本實驗室書面批准。



Certificate of Calibration 校正證書

Certificate No. : C132228
證書編號

ITEM TESTED / 送檢項目 (Job No. / 序引編號 : IC13-0878)

Description / 儀器名稱 : Acoustical Calibrator (EQ081)
Manufacturer / 製造商 : Brüel & Kjær
Model No. / 型號 : 4231
Serial No. / 編號 : 2326408
Supplied By / 委託者 : Action-United Environmental Services and Consulting
Unit A, 20/F., Gold King Industrial Building,
35-41 Tai Lin Pai Road, Kwai Chung, N.T.

TEST CONDITIONS / 測試條件

Temperature / 溫度 : $(23 \pm 2)^{\circ}\text{C}$ Relative Humidity / 相對濕度 : $(55 \pm 20)\%$
Line Voltage / 電壓 : ---

TEST SPECIFICATIONS / 測試規範

Calibration check

DATE OF TEST / 測試日期 : 15 April 2013


TEST RESULTS / 測試結果

The results apply to the particular unit-under-test only.
All results are within manufacturer's specification.
The results are detailed in the subsequent page(s).


The test equipment used for calibration are traceable to National Standards via :

- The Government of The Hong Kong Special Administrative Region Standard & Calibration Laboratory
- Rohde & Schwarz Laboratory, Germany
- Fluke Everett Service Center, USA
- Agilent Technologies, USA

Tested By
測試


K C Lee

Certified By
核證


K M Wu

Date of Issue : 16 April 2013
簽發日期

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準，局部複印本證書需先獲本實驗室書面批准。



Certificate of Calibration

校正證書

Certificate No. : C132228
證書編號

- The unit-under-test (UUT) was allowed to stabilize in the laboratory for over 12 hours before the commencement of the test.
- The results presented are the mean of 3 measurements at each calibration point.
- Test equipment :

<u>Equipment ID</u>	<u>Description</u>	<u>Certificate No.</u>
CL130	Universal Counter	C123541
CL281	Multifunction Acoustic Calibrator	DC110233
TST150A	Measuring Amplifier	C120886

- Test procedure : MA100N.

- Results :

5.1 Sound Level Accuracy

UUT Nominal Value	Measured Value (dB)	Mfr's Spec. (dB)	Uncertainty of Measured Value (dB)
94 dB, 1 kHz	94.0	± 0.2	± 0.2
114 dB, 1 kHz	114.0		

5.2 Frequency Accuracy

UUT Nominal Value (kHz)	Measured Value (kHz)	Mfr's Spec.	Uncertainty of Measured Value (Hz)
1	1.000 0	1 kHz ± 0.1 %	± 0.1

Remark : The uncertainties are for a confidence probability of not less than 95 %.

Note :

The values given in this Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environment changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Sun Creation Engineering Limited shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to the Nation Standards as specified in this certificate. This certificate shall not be reproduced except in full, without the prior written approval of this laboratory.

本證書所載校正用之測試器材均可溯源至國際標準。局部複印本證書需先獲本實驗室書面批准。

Sun Creation Engineering Limited – Calibration & Testing Laboratory

c/o 4/F, Tsing Shan Wan Exchange Building, 1 Hing On Lane, Tuen Mun, New Territories, Hong Kong

輝創工程有限公司 - 校正及檢測實驗室

c/o 香港新界屯門興安里一號青山灣機樓四樓

Tel/電話: 2927 2606 Fax/傳真: 2744 8986 E-mail/電郵: callab@suncreation.com Website/網址: www.suncreation.com



ALS Technichem (HK) Pty Ltd

REPORT OF EQUIPMENT PERFORMANCE CHECK/CALIBRATION

CONTACT: MR BEN TAM
CLIENT: ACTION UNITED ENVIRO SERVICES
ADDRESS: RM A 20/F., GOLDEN KING IND BLDG,
NO. 35-41 TAI LIN PAI ROAD,
KWAI CHUNG,
N.T., HONG KONG

WORK ORDER: HK1309651
LABORATORY: HONG KONG
DATE RECEIVED: 11/04/2013
DATE OF ISSUE: 17/04/2013

PROJECT: --

COMMENTS

It is certified that the item under calibration/checking has been calibrated/checked by corresponding calibrated equipment in the laboratory.

Maximum Tolerance and calibration frequency stated in the report, unless otherwise stated, the internal acceptance criteria of ALS will be followed.

Scope of Test: Dissolved Oxygen, Turbidity, pH, Salinity and Temperature
Equipment Type: SONDE
Brand Name: YSI
Model No.: YSI 6820 / 650MDS
Serial No.: 02J0912/02K0788 AA
Equipment No.: --
Date of Calibration: 16 April, 2013

NOTES


This is the Final Report and supersedes any preliminary report with this batch number.
Results apply to sample(s) as submitted. All pages of this report have been checked and approved for release.

ISSUING LABORATORY: HONG KONG

Address

ALS Technichem (HK) Pty Ltd
11/F Chung Shun Knitting Centre
1-3 Wing Yip Street
Kwai Chung
HONG KONG

Phone: 852-2610 1044
Fax: 852-2610 2021
Email: hongkong@alsglobal.com


Mr. Fung Lim Chee Richard
General Manager
Greater China & Hong Kong

This report may not be reproduced except with prior written approval from ALS Technichem (HK) Pty Ltd.

Page 1 of 2

REPORT OF EQUIPMENT PERFORMANCE CHECK / CALIBRATION

Work Order: HK1309651
Date of Issue: 17/04/2013
Client: ACTION UNITED ENVIRO SERVICES



Equipment Type: SONDE
Brand Name: YSI
Model No.: YSI 6820 / 650MDS
Serial No.: 02J0912/02K0788 AA
Equipment No.: --
Date of Calibration: 16 April, 2013

Date of next Calibration: 16 July, 2013

Parameters:

Dissolved Oxygen

Method Ref: APHA (21st edition), 4500O: G

Expected Reading (mg/L)	Displayed Reading (mg/L)	Tolerance (mg/L)
5.51	7.86	2.35
8.65	8.66	0.01
Tolerance Limit (±mg/L)		0.20

pH Value

Method Ref: APHA 21st Ed. 4500H:B

Expected Reading (pH Unit)	Displayed Reading (pH Unit)	Tolerance (pH unit)
4.0	3.98	-0.02
7.0	6.92	-0.08
10.0	9.97	-0.03
Tolerance Limit (±pH unit)		0.20

Salinity

Method Ref: APHA (21st edition), 2520B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	0.08	--
10	10.83	8.3
20	21.15	5.7
30	32.28	7.6
Tolerance Limit (±%)		10.0

Temperature

Method Ref: Section 6 of International Accreditation New Zealand Technical Guide No. 3 Second edition March 2008: Working Thermometer Calibration Procedure.

Expected Reading (°C)	Displayed Reading (°C)	Tolerance (°C)
12.0	11.40	-0.6
23.0	22.54	-0.5
42.5	42.68	0.2
Tolerance Limit (±°C)		2.0

Turbidity

Method Ref: APHA (21st edition), 2130B

Expected Reading (NTU)	Displayed Reading (NTU)	Tolerance (%)
0	-0.2	--
40	42.6	6.5
80	78.0	-2.5
400	435.5	8.9
800	782.9	-2.1
Tolerance Limit (±%)		10.0

Remark: "Displayed Reading" presents the figures shown on item under calibration / checking regardless of equipment precision or significant figures.

Mr. Fung Lim Chee, Richard
 General Manager -
 Greater China & Hong Kong

Appendix F

Event and Action Plan

Air Quality

EVENT	ACTION ET	IC(E)	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IC(E) and ER; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method. 	<ol style="list-style-type: none"> 1. Notify Contractor. 	<ol style="list-style-type: none"> 1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IC(E) and ER; 3. Advise the ER on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IC(E) and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IC(E) and ER; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Submit proposals for remedial to ER within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.
LIMIT LEVEL				
1. Exceedance for one sample	<ol style="list-style-type: none"> 1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform ER, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results. 	<ol style="list-style-type: none"> 1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ER on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
2. Exceedance for two or more consecutive samples	<ol style="list-style-type: none"> 1. Notify IC(E), ER, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IC(E) and ER to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consolidation with the IC(E), agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Construction Noise

EVENT	ACTION	IC(E)	ER	CONTRACTOR
Action Level	<ol style="list-style-type: none"> 1. Notify IC(E) and Contractor; 2. Carry out investigation; 3. Report the results of investigation to the IC(E), ER and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness 	<ol style="list-style-type: none"> 1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented. 	<ol style="list-style-type: none"> 1. Submit noise mitigation proposals to IC(E); 2. Implement noise mitigation proposals.
Limit Level	<ol style="list-style-type: none"> 1. Identify source; 2. Inform IC(E), ER, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IC(E), ER and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IC(E), EPD and ER informed of the results; 8. If exceedance stops, cease additional monitoring. 	<ol style="list-style-type: none"> 1. Discuss amongst ER, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the ER accordingly; 3. Supervise the implementation of remedial measures. 	<ol style="list-style-type: none"> 1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated. 	<ol style="list-style-type: none"> 1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IC(E) within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the ER until the exceedance is abated.

Water Quality

EVENT	ACTION			
	ET	IC(E)	ER	CONTRACTOR
ACTION LEVEL				
1. Exceedance for one sampling day	<ol style="list-style-type: none"> Repeat in-situ measurement on the next day of exceedance to confirm findings; Identify source(s) of impact; Inform ICE, Contractor, ER, EPD and AFCD; and Check monitoring data, all plant, equipment and Contractor's working methods. 	<ol style="list-style-type: none"> Check monitoring data submitted by ET and Contractor's working methods 	<ol style="list-style-type: none"> Confirm receipt of notification of non-compliance in writing; and Notify Contractor 	<ol style="list-style-type: none"> Information the ER and confirm notification of the non-compliance in writing; Rectify unacceptable practice; and Amend working methods if appropriate
2. Exceedance for two or more consecutive sampling days	<ol style="list-style-type: none"> Same as the above; Inform ICE, Contractor, ER, EPD and AFCD; Discuss mitigation measures with IC(E), RE and Contractor; Ensure well implementation of mitigation measures; and Increase the monitoring frequency to daily until no exceedance of Action Level 	<ol style="list-style-type: none"> Same as the above; Discuss with ET and Contractor on possible remedial actions; Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly; and Supervise the implementation of mitigation measures. 	<ol style="list-style-type: none"> Discuss with IC(E) on the proposed mitigation measures; Ensure well implementation of mitigation measures; and Assess the effectiveness of the implemented mitigation measures 	<ol style="list-style-type: none"> Same as the above; Check all plant and equipment and consider changes of working methods; Submit proposal of additional mitigation measures to ER within 3 working days of notification and discuss with ET, IC(E), and ER; and Implement the agreed mitigation measures
LIMIT LEVEL				
1. Exceedance for one sampling day	<ol style="list-style-type: none"> Repeat in-situ measurement on the next day of exceedance to confirm findings; Identify source(s) of impact; Inform ICE, Contractor, ER, EPD and AFCD; Check monitoring data, all plant, equipment and Contractor's working methods; and Discuss mitigation measures with IC(E), RE and Contractor 	<ol style="list-style-type: none"> Check monitoring data submitted by ET and Contractor's working method Discuss with ER and Contractor on possible remedial actions; and Review the proposed mitigation measures submitted by Contractor and advise the ER accordingly 	<ol style="list-style-type: none"> Confirm receipt of notification failure in writing; and Discuss with IC(E), ET and Contractor on the proposed mitigation measures; and Request Contractor to review the working methods 	<ol style="list-style-type: none"> Inform the ER and confirm notification of the failure in writing; Rectify unacceptable practice; Check all plant and equipment and consider changes of working methods; and Submit proposal of mitigation measures to ER within 3 working days of notification and discuss with ET and ER
2. Exceedance for two or more consecutive sampling days	<ol style="list-style-type: none"> Same as the above; Ensure mitigation measures are implemented; and Increase the monitoring frequency to daily until no exceedance of Limit Level for two consecutive days 	<ol style="list-style-type: none"> Same as the above; and Supervise the Implementation of mitigation measures 	<ol style="list-style-type: none"> Same as the above; Ensure well implementation of mitigation measures Make agreement on the mitigation measures to be implemented; and Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of limit level 	<ol style="list-style-type: none"> Same as the above; Take immediate action to avoid further exceedance; Implement the agreed mitigation measures; Resubmit proposals of mitigation measures if problem still not under control; and As directed by the Engineer, to slow down or to stop all or part of the construction activities until to no exceedance of Limit Level.

Coral Monitoring

EVENT	ACTION	CONTRACTOR	ER/ IC(E)
	ET	CONTRACTOR	ER/ IC(E)
Action Level being exceeded	<p>Inform contractor, AFCD and EPD immediately;</p> <p>Discuss mitigation measure with ER/IC(E) and Contractor;</p> <p>Ensure mitigation measures are implemented.</p>	<p>Inform the Engineer and confirm notification of the non-compliance in writing;</p> <p>Propose mitigation measure to ER/IC(E) within 1 working day and discuss with Et and ER/IC(E);</p> <p>Ensure mitigation measures are implemented.</p>	<p>Inform contractor, Review water quality monitoring data;</p> <p>Determine whether water quality monitoring data shows effects attributable to the backfilling works;</p> <p>If water quality monitoring data indicates effects attributable to backfilling works, then make agreement on mitigation measures to be implemented;</p> <p>If water quality monitoring data indicates no effects attributable to backfilling works then Action Level is not triggered;</p> <p>Assess the effectiveness of the implemented mitigation measures.</p>
Limit Level	<p>Inform contractor, AFCD and EPD immediately;</p> <p>Discuss mitigation measure with ER/IC(E) and Contractor;</p> <p>Ensure mitigation measures are implemented.</p>	<p>Inform the Engineer and confirm notification of the non-compliance in writing;</p> <p>Suspend backfilling operations;</p> <p>Propose mitigation measure to ER/IC(E) within 3 working days and discuss with Et and ER/IC(E);</p> <p>Implement the agreed mitigation measures.</p>	<p>Inform contractor to suspend backfilling operations;</p> <p>Make agreement on the mitigation measures to be implemented;</p> <p>Assess the effectiveness of the implemented mitigation measures.</p>

Appendix G

Monitoring Data Sheet

24-hour TSP Monitoring Data Sheet

Air Quality Monitoring - 24-hour TSP monitoring data for Yung Shue Wan

24-hour TSP Monitoring Results - AC02b

DATE	ELAPSED TIME		CHART READING					AVG TEMP (oC)	STANDARD			INITIAL FILTER WEIGHT (g)	FINAL FILTER WEIGHT (g)	WEIGHT DUST COLLECTED (g)	DUST 24-hour TSP IN AIR (ug/m ³)
	SAMPLE NUMBER	INITIAL	FINAL	ACTUAL (min)	MIN	MAX	AVG		AVG PRESS (hPa)	FLOW RATE (m3/min)	AIR VOLUME (std m3)				
2-May-13	25469	6255.07	6279.06	1439.40	32	33	32.5	24.8	1010.9	0.62	898	3.6005	3.6931	0.0926	103
8-May-13	25472	6279.06	6303.05	1439.40	30	32	31.0	25.4	1010.2	0.57	816	3.6036	3.6236	0.0200	25
14-May-13	25553	6303.05	6327.04	1439.40	29	30	29.5	26.2	1010	0.51	734	3.6047	3.6736	0.0689	94
20-May-13	25555	6327.04	6351.03	1439.40	29	31	30.0	26.1	1008.5	0.53	759	3.6476	3.6736	0.0260	34
25-May-13	25561	6351.03	6375.02	1439.40	30	31	30.5	26.4	1008.2	0.55	785	3.6452	3.6694	0.0242	31

Action Level: 161ug/m³

Limit Level: 260ug/m³

24-hour TSP Monitoring Results - AC04c

DATE	ELAPSED TIME		CHART READING					AVG TEMP (oC)	STANDARD			INITIAL FILTER WEIGHT (g)	FINAL FILTER WEIGHT (g)	WEIGHT DUST COLLECTED (g)	DUST 24-hour TSP IN AIR (ug/m ³)
	SAMPLE NUMBER	INITIAL	FINAL	ACTUAL (min)	MIN	MAX	AVG		AVG PRESS (hPa)	FLOW RATE (m3/min)	AIR VOLUME (std m3)				
2-May-13	25470	9248.19	9272.18	1439.40	32	33	32.5	24.8	1010.9	0.75	1084	3.606	3.6384	0.0324	30
8-May-13	25471	9272.18	9296.17	1439.40	30	32	31.0	25.4	1010.2	0.71	1019	3.5927	3.6058	0.0131	13
14-May-13	25552	9296.17	9320.16	1439.40	28	30	29.0	26.2	1010	0.65	932	3.6763	3.6878	0.0115	12
20-May-13	25556	9320.16	9344.15	1439.40	28	30	29.0	26.1	1008.5	0.65	931	3.6503	3.6637	0.0134	14
25-May-13	25562	9344.15	9368.14	1439.40	28	30	29.0	26.4	1008.2	0.65	931	3.6472	3.66	0.0128	14

Action Level: 176ug/m³

Limit Level: 260ug/m³

Marine Water Quality Monitoring Data Sheet

Contract No. DC/2009/13

Construction of Sewage Treatment Works
at Yung Shue Wan and Sok Kwu Wan



Marine Water Quality Monitoring Result at Yung Shue Wan

Date 26-Apr-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/4/26 12:32	WY1	ME	829166	809543	4.3	1.000	21.69	8.53	117.9	2.07	33.69	8.31	3.3
						1.000	21.68	8.93	123.6	2.15	33.72	8.27	
						3.300	21.60	8.45	116.8	2.48	33.96	8.21	
						3.300	21.59	8.25	114.0	2.37	33.96	8.20	
2013/4/26 12:53	WY2	ME	829010	810426	7.5	1.000	21.64	6.79	93.9	1.92	33.91	8.23	2.6
						1.000	21.63	6.99	96.7	1.84	33.89	8.20	
						3.750	21.59	7.07	97.9	1.97	34.09	8.16	6.6
						3.750	21.59	7.13	98.6	2.02	34.10	8.16	
						6.500	21.56	7.19	98.8	1.73	32.91	8.12	8.4
						6.500	21.58	7.17	99.2	1.77	34.26	8.13	
2013/4/26 12:40	WY3	ME	829187	809856	4.6	1.000	21.62	7.63	105.6	2.21	33.99	8.13	4
						1.000	21.58	7.72	106.0	2.17	32.82	8.13	
						3.600	21.59	7.59	104.3	2.66	32.86	8.12	3
						3.600	21.61	7.54	104.5	2.58	34.18	8.13	
2013/4/26 13:10	CY1	ME	828024	808807	12.3	1.000	21.57	7.23	99.3	1.67	32.91	8.26	6
						1.000	21.59	7.70	106.9	1.66	34.59	8.25	
						6.150	21.60	7.78	108.0	1.78	34.62	8.23	6.9
						6.150	21.57	7.72	107.2	1.74	34.70	8.19	
						11.300	21.53	7.52	103.3	1.82	33.56	8.15	7.5
						11.300	21.54	7.49	103.9	1.82	35.33	8.16	
2013/4/26 12:12	CY2	ME	828028	808813	15.8	1.000	21.58	7.31	100.5	1.79	32.99	8.10	3.3
						1.000	21.61	7.34	102.0	1.85	34.62	8.12	
						7.900	21.37	7.33	101.8	1.96	35.28	8.12	3.1
						7.900	21.39	7.22	100.2	2.04	35.28	8.15	
						14.800	21.41	7.05	97.0	0.12	33.78	8.07	3.1
						14.800	21.44	7.01	97.6	2.22	35.52	8.09	
2013/4/26 17:06	WY1	MF	829172	809563	5.3	1.000	21.43	6.76	94.1	1.63	35.57	8.13	10.2
						1.000	21.40	6.76	94.0	1.68	35.59	8.10	
						4.300	21.30	6.59	91.5	1.81	35.72	8.09	9.2
						4.300	21.31	6.57	91.4	1.80	35.71	8.08	
2013/4/26 17:26	WY2	MF	829013	810387	8.4	1.000	21.55	7.33	101.5	1.45	34.27	8.09	3.3
						1.000	21.55	7.27	100.7	1.43	34.33	8.11	
						4.200	21.64	7.26	101.3	1.51	35.35	8.17	3.7
						4.200	21.61	7.16	99.9	1.63	35.45	8.13	
						7.400	21.31	7.38	102.7	1.29	35.89	8.14	2.9
						7.400	21.28	7.34	102.1	1.36	35.92	8.13	
2013/4/26 17:16	WY3	MF	829194	809866	5.5	1.000	21.52	7.15	99.6	1.74	35.59	8.30	3
						1.000	21.49	7.23	100.7	1.82	35.62	8.27	
						4.500	21.50	6.95	96.8	1.85	35.60	8.20	2.7
						4.500	21.73	6.77	94.3	1.86	34.71	8.19	
2013/4/26 17:42	CY1	MF	828407	810824	13.5	1.000	21.58	7.42	102.1	1.28	33.14	8.31	2.6
						1.000	21.57	7.96	109.0	1.25	32.34	8.25	
						6.750	21.48	8.00	110.0	1.37	33.36	8.18	3.4
						6.750	21.48	7.91	108.9	1.42	33.39	8.16	
						12.500	21.49	7.69	106.1	1.31	33.92	8.17	3.9
						12.500	21.50	7.62	105.3	1.29	34.07	8.17	
2013/4/26 18:02	CY2	MF	828016	808819	16.6	1.000	21.83	7.99	111.9	1.31	35.37	8.06	5.6
						1.000	21.83	8.19	114.7	1.36	35.37	8.00	
						8.300	21.76	8.44	118.0	1.48	35.20	7.90	5.9
						8.300	21.78	8.36	117.0	1.52	35.49	7.89	
						15.600	21.20	8.30	115.3	1.69	35.86	7.84	4.4
						15.600	21.16	8.23	113.8	1.74	35.28	7.81	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 30-Apr-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/4/30 15:13	WY1	ME	829179	809543	5.2	1.000	22.83	6.60	93.4	1.04	34.20	8.28	5.5
						1.000	22.84	6.59	93.4	0.99	34.22	8.26	
						4.200	23.24	6.50	93.0	1.24	34.69	8.27	
						4.200	23.12	6.40	91.2	1.26	34.55	8.27	
2013/4/30 15:36	WY2	ME	828983	810391	8.4	1.000	22.96	6.23	88.4	1.37	34.22	8.20	3
						1.000	23.01	6.23	88.5	1.43	34.25	8.20	
						4.200	23.22	6.21	88.6	1.58	34.57	8.22	3.9
						4.200	23.25	6.11	87.4	1.49	34.82	8.23	
						7.400	22.55	6.41	91.0	1.32	35.53	8.20	
						7.400	22.23	6.36	89.9	1.37	35.78	8.20	
2013/4/30 15:23	WY3	ME	829208	809837	5.6	1.000	23.07	6.86	97.6	1.07	34.34	8.23	2.6
						1.000	23.02	6.11	86.7	1.13	34.19	8.22	
						4.600	23.30	6.55	93.8	1.34	34.94	8.24	4.9
						4.600	23.38	6.40	91.9	1.35	34.89	8.25	
2013/4/30 15:54	CY1	ME	828414	810811	13.6	1.000	22.53	6.61	92.5	1.36	33.20	8.19	1.7
						1.000	22.51	6.66	93.2	1.24	33.25	8.17	
						6.800	22.13	6.52	91.1	1.15	34.21	8.13	3
						6.800	22.11	6.63	92.8	1.23	34.26	8.14	
						12.600	22.09	6.09	85.3	1.09	34.48	8.10	2.9
						12.600	22.09	6.12	85.7	1.27	34.44	8.09	
2013/4/30 14:54	CY2	ME	828017	808816	17.6	1.000	24.50	7.49	110.0	1.34	35.52	7.58	2.8
						1.000	24.32	8.43	123.5	1.37	35.57	7.38	
						8.800	22.29	8.57	121.5	1.49	36.09	6.92	2.4
						8.800	22.29	8.42	119.4	1.36	36.05	6.85	
						16.600	21.81	8.19	115.1	1.18	36.13	6.63	
						16.600	21.80	8.16	114.7	1.22	36.17	6.65	
2013/4/30 8:15	WY1	MF	829164	809561	4.1	1.000	22.59	6.99	98.9	1.32	34.85	7.27	5.9
						1.000	22.58	6.91	97.8	1.45	35.04	7.27	
						3.100	21.96	6.55	92.2	1.61	35.93	7.22	8.8
						3.100	21.95	6.46	91.0	1.58	35.94	7.22	
2013/4/30 8:37	WY2	MF	829010	810411	7.6	1.000	22.41	7.05	99.9	1.14	35.67	7.58	3.3
						1.000	22.44	7.34	104.0	1.28	35.65	7.54	
						3.800	21.98	6.69	94.3	1.31	36.01	7.47	7.4
						3.800	21.87	6.59	92.7	1.26	36.08	7.45	
						6.600	21.84	7.09	99.7	1.09	36.08	7.41	8.1
						6.600	21.82	6.55	92.2	1.20	36.15	7.41	
2013/4/30 8:26	WY3	MF	829184	809861	4.5	1.000	22.64	6.50	92.1	1.26	34.88	7.15	5.2
						1.000	22.60	6.26	88.8	1.37	35.21	7.21	
						3.500	21.94	5.59	78.8	1.49	36.00	7.13	8.3
						3.500	21.93	5.69	80.1	1.56	35.90	7.14	
2013/4/30 8:53	CY1	MF	828421	810829	12.7	1.000	23.28	6.74	96.6	0.98	35.06	7.79	3.7
						1.000	23.29	6.61	94.7	1.13	34.97	7.80	
						6.350	22.01	6.90	97.4	0.87	36.11	7.73	4.5
						6.350	21.97	6.80	95.8	0.96	36.07	7.69	
						11.700	21.77	6.32	88.9	1.04	36.13	7.56	4.4
						11.700	21.77	6.24	87.6	1.12	36.13	7.57	
2013/4/30 9:14	CY2	MF	828022	808813	16.5	1.000	23.07	7.64	109.4	1.16	35.41	7.95	4.3
						1.000	23.07	7.48	107.2	1.21	35.44	7.96	
						8.250	22.10	6.94	98.1	1.03	36.11	7.81	4.1
						8.250	22.11	6.86	96.9	1.09	36.11	7.79	
						15.500	21.76	6.09	85.6	0.84	36.16	7.69	
15.500	21.77	5.78	81.2	0.92	36.16	7.67	4.9						

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 2-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/2 17:25	WY1	ME	829159	809557	4.3	1.000	22.38	7.28	102.4	2.17	34.48	8.07	4.2
						1.000	22.45	7.28	102.7	2.11	34.78	8.06	
						3.300	23.17	7.71	110.5	2.36	35.29	8.14	6.7
						3.300	23.16	7.72	110.9	2.39	35.77	8.16	
2013/5/3 17:49	WY2	ME	829006	810413	7.7	1.000	22.22	7.76	108.6	2.01	34.07	8.09	4.9
						1.000	22.26	7.66	107.6	1.96	34.63	8.09	
						3.850	23.06	7.77	111.3	1.97	35.53	8.15	5.2
						3.850	23.02	7.59	108.7	1.86	35.72	8.17	
						6.700	21.91	8.20	115.4	2.14	36.00	8.16	4.4
						6.700	21.93	8.29	116.7	2.05	35.98	8.13	
2013/5/3 17:36	WY3	ME	829196	809834	4.6	1.000	22.44	7.55	106.5	2.08	34.86	8.10	5.2
						1.000	22.58	7.70	109.0	2.15	35.01	8.11	
						3.600	23.07	8.05	115.6	2.29	35.81	8.17	5.3
						3.600	23.08	8.14	116.8	2.37	35.74	8.18	
2013/5/3 18:07	CY1	ME	828422	810822	11.9	1.000	22.13	7.74	108.5	2.03	34.61	8.19	4.6
						1.000	22.09	7.88	110.4	1.91	34.57	8.16	
						5.950	21.91	8.45	118.9	1.83	35.95	8.16	5
						5.950	21.91	8.56	120.5	1.79	35.97	8.17	
						10.900	21.88	8.37	117.3	1.74	35.29	8.05	17.6
						10.900	21.88	8.34	117.0	1.88	35.51	8.08	
2013/5/3 17:07	CY2	ME	828024	808810	15.9	1.000	23.07	7.36	103.0	1.69	31.43	8.46	5
						1.000	23.02	7.34	102.7	1.82	31.50	8.41	
						7.950	21.99	7.29	101.1	1.96	33.22	8.31	4.6
						7.950	21.96	7.40	102.5	2.02	33.04	8.28	
						14.900	21.88	7.45	104.8	1.54	35.98	8.21	5.4
						14.900	21.88	7.36	103.5	1.63	35.98	8.20	
2013/5/3 10:32	WY1	MF	829177	809558	5.3	1.000	21.77	7.61	105.8	1.86	34.25	8.26	4.1
						1.000	21.78	7.36	102.3	1.89	34.25	8.22	
						4.300	21.77	6.86	96.0	1.91	35.44	8.21	7.1
						4.300	21.79	6.77	94.7	1.99	35.43	8.20	
2013/5/3 10:07	WY2	MF	829011	810393	8.7	1.000	21.88	7.71	107.3	1.82	34.21	8.22	3.4
						1.000	21.88	7.56	105.2	1.93	34.09	8.22	
						4.350	21.85	7.47	104.3	1.67	34.83	8.17	5.5
						4.350	21.85	7.38	103.0	1.74	34.85	8.16	
						7.700	21.84	7.39	103.8	1.59	35.70	8.13	5.4
						7.700	21.85	7.35	103.0	1.71	35.39	8.08	
2013/5/3 10:22	WY3	MF	829192	809861	5.6	1.000	21.83	7.45	102.3	1.96	31.96	8.35	4.2
						1.000	21.83	7.28	99.9	1.81	31.94	8.32	
						4.600	21.81	7.10	99.1	1.94	34.84	8.24	7.7
						4.600	21.80	6.95	96.9	2.03	34.86	8.20	
2013/5/3 9:50	CY1	MF	828387	810774	13.6	1.000	21.77	7.19	99.7	1.62	33.72	8.48	5
						1.000	21.77	7.22	100.0	1.71	33.74	8.41	
						6.800	21.84	7.50	104.6	1.83	34.67	8.29	5.7
						6.800	21.85	7.54	105.0	1.88	34.48	8.24	
						12.600	21.90	7.41	104.1	1.51	35.72	8.16	5.4
						12.600	21.90	7.31	102.8	1.54	35.74	8.12	
2013/5/3 10:47	CY2	MF	828017	808820	16.8	1.000	22.81	6.70	95.6	1.53	35.69	8.44	4.9
						1.000	22.73	6.57	93.6	1.67	35.70	8.42	
						8.400	21.92	6.56	92.3	1.74	35.93	8.20	5.5
						8.400	21.92	6.56	92.3	1.82	35.93	8.19	
						15.800	21.89	6.93	97.5	1.44	35.98	8.17	7.2
						15.800	21.90	6.81	95.9	1.39	35.98	8.17	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 4-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/4 9:19	WY1	ME	829177	809542	4.3	1.000	21.78	7.06	99.4	2.07	36.33	8.27	8
						1.000	21.76	7.12	100.1	2.28	36.36	8.23	
						3.300	21.76	7.03	98.9	2.31	36.38	8.24	8.1
						3.300	21.76	7.06	99.3	2.16	36.39	8.24	
2013/5/4 8:58	WY2	ME	828988	810387	7.7	1.000	21.63	7.42	102.6	1.73	33.74	8.46	7.3
						1.000	21.63	7.34	102.6	1.78	35.59	8.41	
						3.850	21.65	7.30	102.6	1.64	36.35	8.34	7.2
						3.850	21.65	7.31	102.6	1.75	36.35	8.32	
						6.700	21.63	7.30	102.6	1.48	36.60	8.29	7.3
						6.700	21.63	5.84	82.1	1.46	36.61	8.26	
2013/5/4 9:10	WY3	ME	829205	809867	4.5	1.000	21.76	7.28	102.4	1.86	36.33	8.42	2.4
						1.000	21.77	7.28	102.4	1.93	36.32	8.38	
						3.500	21.75	7.28	102.5	1.97	36.40	8.33	3.9
						3.500	21.74	7.28	102.5	2.10	36.40	8.31	
2013/5/4 8:40	CY1	ME	828410	810821	12.3	1.000	21.65	7.36	102.6	1.58	35.10	8.32	4
						1.000	21.63	7.36	102.6	1.66	35.13	8.24	
						6.150	21.70	7.16	100.5	1.43	36.06	8.14	3.6
						6.150	21.72	7.15	100.3	1.62	35.98	8.15	
						11.300	21.62	7.08	99.5	1.52	36.69	8.14	3.1
						11.300	21.61	7.00	98.4	1.59	36.69	8.13	
2013/5/4 9:36	CY2	ME	828011	808820	16.1	1.000	21.70	7.36	102.5	1.71	34.75	8.29	3.2
						1.000	21.70	7.36	102.5	1.74	34.80	8.25	
						8.050	22.45	6.90	98.1	1.86	36.12	8.27	4
						8.050	22.03	6.95	98.3	1.93	36.29	8.26	
						15.100	21.61	6.95	97.5	1.64	36.54	8.21	6.1
						15.100	21.61	6.86	96.3	1.62	36.54	8.19	
2013/5/4 13:31	WY1	MF	829183	809572	5.3	1.000	21.82	7.32	102.4	1.57	35.20	8.25	6.9
						1.000	21.82	7.32	102.4	1.69	35.21	8.17	
						4.300	21.77	7.31	102.4	1.72	35.60	8.01	6.2
						4.300	21.76	7.31	102.4	1.66	35.61	7.98	
2013/5/4 13:53	WY2	MF	829014	810406	8.8	1.000	21.81	7.40	102.4	1.46	33.44	8.29	6.1
						1.000	21.85	7.31	102.3	1.51	35.36	8.26	
						4.400	21.75	7.32	102.5	1.62	35.65	8.14	5.3
						4.400	21.75	7.31	102.5	1.47	35.63	8.13	
						7.800	21.70	7.18	99.6	1.31	34.17	8.02	5.1
						7.800	21.71	7.16	100.4	1.39	35.97	8.01	
2013/5/4 13:43	WY3	MF	829206	809838	5.5	1.000	21.78	7.32	102.4	1.74	35.39	8.31	5.7
						1.000	21.81	7.31	102.4	1.63	35.36	8.26	
						4.500	21.80	7.31	102.4	1.82	35.43	8.15	5.1
						4.500	21.79	7.39	102.4	1.85	33.77	8.09	
2013/5/4 14:10	CY1	MF	828422	810805	13.6	1.000	21.78	7.34	102.4	1.24	34.92	8.28	2.6
						1.000	21.76	7.34	102.4	1.35	34.95	8.24	
						6.800	21.76	7.33	102.4	1.38	35.22	8.14	3.7
						6.800	21.66	7.38	102.5	1.26	34.51	8.08	
						12.600	21.68	7.03	98.7	1.14	36.34	8.10	5.1
						12.600	21.75	7.18	100.4	1.17	35.32	8.12	
2013/5/4 13:12	CY2	MF	828024	808816	17.6	1.000	22.73	7.14	101.3	1.37	35.00	7.81	4.3
						1.000	22.45	7.20	101.7	1.28	34.81	7.76	
						8.800	21.67	7.14	100.3	1.19	36.47	7.58	4.8
						8.800	21.67	6.60	92.7	1.16	36.48	7.56	
						16.600	21.60	6.77	95.1	1.22	36.68	7.47	4.7
						16.600	21.58	6.87	95.6	1.27	35.18	7.43	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 6-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/6 10:46	WY1	ME	829174	809562	4.3	1.000	22.09	6.99	98.6	2.72	35.80	7.88	2.6
						1.000	22.12	6.94	98.0	2.83	35.80	7.90	
						3.300	22.03	6.97	98.3	2.82	36.00	7.88	
						3.300	22.00	7.00	97.9	3.08	34.66	7.83	
2013/5/6 11:06	WY2	ME	829007	810412	7.8	1.000	22.00	7.39	103.2	2.38	34.46	8.19	3.5
						1.000	22.01	7.21	101.5	2.33	35.82	8.15	
						3.900	21.90	6.80	95.8	2.15	36.20	8.06	6.5
						3.900	21.87	6.78	95.5	2.29	36.19	8.04	
						6.800	21.62	6.77	95.1	2.06	36.61	7.98	
						6.800	21.64	6.66	93.6	2.24	36.59	7.98	
2013/5/6 10:55	WY3	ME	829213	809847	4.5	1.000	22.21	6.85	96.9	2.61	35.76	7.77	5.6
						1.000	22.14	6.88	97.1	2.66	35.81	7.76	
						3.500	22.02	6.87	96.9	2.84	36.16	7.77	
						3.500	22.02	6.84	96.6	2.91	36.11	7.75	
2013/5/6 11:21	CY1	ME	828409	810813	12.5	1.000	21.93	6.78	95.6	1.95	36.09	8.04	6.4
						1.000	21.96	6.78	95.6	1.98	36.09	8.05	
						6.250	21.76	6.78	95.2	2.01	36.22	7.94	8.9
						6.250	21.74	6.72	94.4	2.07	36.23	7.92	
						11.500	21.75	6.67	93.7	1.84	36.26	7.92	
						11.500	21.74	6.65	93.5	1.92	36.27	7.88	
2013/5/6 10:29	CY2	ME	828019	808817	15.6	1.000	22.09	6.36	89.4	2.03	35.38	8.03	3.4
						1.000	22.06	6.49	90.4	2.14	33.60	8.01	
						7.800	21.95	6.74	95.0	2.33	36.21	7.98	4.5
						7.800	21.95	6.78	95.6	2.18	36.20	7.95	
						14.600	21.63	7.23	101.5	1.96	36.45	7.93	
						14.600	21.64	7.28	102.3	2.05	36.45	7.92	
2013/5/6 16:12	WY1	MF	829164	809566	5.2	1.000	22.10	6.95	98.5	1.90	36.57	8.24	9.2
						1.000	22.09	6.98	97.9	1.87	34.84	8.16	
						4.200	22.06	6.54	92.7	2.09	36.71	8.06	
						4.200	22.06	6.50	92.1	2.23	36.68	8.01	
2013/5/6 16:34	WY2	MF	829002	810423	8.5	1.000	22.26	6.96	98.7	1.69	36.23	8.12	3.6
						1.000	22.25	6.88	96.5	1.77	34.40	8.08	
						4.250	22.20	7.06	98.9	1.86	34.47	8.07	8.2
						4.250	22.23	6.87	97.4	1.63	36.26	8.08	
						7.500	22.21	6.82	96.7	1.47	36.31	8.08	
						7.500	22.20	6.90	97.9	1.56	36.29	8.06	
2013/5/6 16:20	WY3	MF	829191	809858	5.4	1.000	22.16	6.58	93.3	1.97	36.37	8.27	7.4
						1.000	22.16	6.44	91.2	2.04	36.37	8.22	
						4.400	21.95	6.06	85.6	2.15	36.53	8.13	
						4.400	21.94	6.11	86.3	2.32	36.51	8.09	
2013/5/6 16:50	CY1	MF	828419	810820	13.6	1.000	22.39	7.33	103.7	1.42	35.63	8.25	2.7
						1.000	22.39	7.32	103.8	1.46	35.70	8.23	
						6.800	22.85	6.79	97.2	1.37	36.24	8.22	3.4
						6.800	22.75	6.78	97.0	1.51	36.27	8.20	
						12.600	21.78	6.83	96.2	1.22	36.51	8.11	
						12.600	21.79	6.75	95.1	1.26	36.49	8.10	
2013/5/6 15:52	CY2	MF	828022	808813	16.8	1.000	22.07	6.66	94.0	1.65	36.00	7.82	8.5
						1.000	22.06	6.70	94.5	1.71	36.06	7.79	
						8.400	22.02	6.49	92.1	1.49	37.12	7.69	8.6
						8.400	22.03	6.45	91.6	1.32	37.15	7.67	
						15.800	21.68	6.32	88.7	1.29	36.07	7.57	
						15.800	21.68	6.29	89.0	1.37	37.57	7.57	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 8-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/8 11:06	WY1	ME	829177	809561	4.4	1.000	23.50	7.39	100.2	2.85	35.99	7.64	7.1
						1.000	23.50	7.73	104.1	1.97	34.91	7.60	
						3.400	23.50	7.92	107.5	2.11	36.03	7.60	
						3.400	23.50	7.82	106.1	2.18	36.03	7.60	
2013/5/8 11:29	WY2	ME	828984	810392	8.7	1.000	23.50	7.75	104.8	1.79	35.62	7.56	6.7
						1.000	23.50	7.83	105.8	1.90	35.62	7.55	
						4.350	23.50	7.88	106.9	1.99	36.23	7.57	6.6
						4.350	23.50	7.86	106.1	2.08	35.69	7.54	
						7.700	23.50	7.75	104.3	2.38	35.30	7.53	
2013/5/8 11:17	WY3	ME	829183	809847	4.6	1.000	23.50	8.06	109.2	1.82	36.02	7.57	5.7
						1.000	23.50	7.95	107.7	1.94	35.99	7.56	
						3.600	23.50	7.79	105.6	2.13	36.15	7.56	
						3.600	23.50	7.72	104.6	2.22	36.15	7.56	
2013/5/8 11:35	CY1	ME	828414	810822	12.5	1.000	23.50	7.96	107.3	1.57	35.92	7.58	4.9
						1.000	23.50	7.87	105.5	1.69	35.11	7.55	
						6.250	23.50	7.99	107.1	1.72	34.99	7.54	6.1
						6.250	23.50	7.88	105.8	1.61	35.41	7.53	
						11.500	23.50	7.91	106.8	1.64	36.34	7.56	
2013/5/8 11:58	CY2	ME	828021	808817	15.9	1.000	24.00	7.48	102.0	1.66	35.92	7.54	8.9
						1.000	24.00	7.68	105.0	1.75	35.89	7.54	
						7.950	24.00	8.14	109.5	1.82	35.38	7.48	8.5
						7.950	24.00	8.09	109.2	1.76	36.01	7.47	
						14.900	24.00	8.18	110.6	1.70	36.12	7.49	
2013/5/8 17:06	WY1	MF	829173	808558	5.2	1.000	24.00	8.65	117.7	1.67	35.75	7.87	9
						1.000	24.00	8.45	114.8	1.79	35.44	7.82	
						4.200	24.00	8.45	114.6	1.74	36.23	7.79	
						4.200	24.00	8.27	112.3	1.88	36.20	7.79	
2013/5/8 17:26	WY2	MF	829013	810415	9.6	1.000	24.00	8.47	115.3	1.73	36.23	7.75	12.9
						1.000	24.00	8.54	116.4	1.75	36.21	7.75	
						4.800	24.00	8.68	118.1	1.81	36.16	7.73	12.4
						4.800	24.00	8.63	117.3	1.73	36.15	7.73	
						8.600	23.50	8.63	116.5	1.76	36.01	7.70	
2013/5/8 17:15	WY3	MF	829201	809874	5.4	1.000	23.50	8.64	116.6	1.84	36.13	7.71	13.9
						1.000	24.00	8.34	113.2	1.58	35.65	7.79	
						4.400	24.00	8.76	119.0	1.71	35.84	7.77	
						4.400	24.00	8.69	118.0	1.64	36.21	7.76	
2013/5/8 17:40	CY1	MF	828422	810810	13.2	1.000	24.00	8.79	118.8	1.79	35.58	7.74	10.6
						1.000	24.00	9.00	122.3	1.46	36.22	7.87	
						6.600	23.50	8.81	119.2	1.55	36.06	7.75	
						6.600	23.50	8.96	121.1	1.59	36.13	7.74	
						12.200	23.00	8.93	119.3	1.42	34.03	7.66	
2013/5/8 18:02	CY2	MF	828016	808827	16.8	1.000	23.00	8.82	119.2	1.50	36.11	7.70	20.5
						1.000	24.00	9.08	123.9	1.56	36.29	7.78	
						1.000	24.00	8.15	111.3	1.44	36.13	7.79	
						8.400	23.50	8.37	113.5	1.39	36.12	7.77	
						8.400	23.50	8.08	109.5	1.31	36.16	7.75	
						15.800	23.00	8.08	109.3	1.24	36.14	7.73	
2013/5/8 18:02	CY2	MF	828016	808827	16.8	15.800	23.00	8.02	108.4	1.36	36.22	7.72	15.2
						15.800	23.00	8.02	108.4	1.36	36.22	7.72	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 10-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/10 12:21	WY1	ME	829184	809555	4.8	1.000	27.50	10.17	123.6	3.61	25.03	8.57	4.8
						1.000	27.50	10.00	121.5	3.73	24.96	8.60	
						3.800	27.30	8.79	114.4	3.82	33.08	8.63	
						3.800	27.30	8.72	114.4	3.88	34.07	8.69	
2013/5/10 12:42	WY2	ME	829018	810387	8.9	1.000	27.60	8.70	114.4	2.58	34.31	8.80	2.9
						1.000	27.60	8.71	114.5	2.31	34.31	8.82	
						4.450	27.50	8.53	112.0	2.41	34.35	8.91	
						4.450	27.50	8.53	112.1	2.43	34.36	8.91	
2013/5/10 12:30	WY3	ME	829196	809857	5.1	1.000	27.20	8.29	108.5	2.20	33.98	8.93	5.3
						1.000	27.20	8.29	108.5	2.28	33.91	8.94	
						4.100	27.20	8.45	111.6	3.57	34.25	8.66	
						4.100	27.20	8.44	111.5	3.74	34.44	8.81	
2013/5/10 12:56	CY1	ME	828424	810809	13	1.000	27.80	8.75	113.5	2.19	33.96	8.83	1.5
						1.000	27.80	8.68	112.7	2.25	33.95	8.84	
						6.500	27.40	8.49	110.0	2.08	33.61	8.83	
						6.500	27.40	8.50	110.8	2.16	34.21	8.87	
2013/5/10 13:11	CY2	ME	828015	808824	16.5	12.000	27.00	8.51	111.1	2.05	34.23	8.90	4
						12.000	27.00	8.57	111.7	2.02	34.26	8.89	
						1.000	27.80	8.47	110.3	2.22	33.63	8.42	
						1.000	27.80	8.49	111.2	2.13	34.07	8.48	
2013/5/10 8:50	WY1	MF	829173	809541	5.4	1.000	26.20	6.36	85.0	2.26	34.41	8.16	2.9
						1.000	26.20	6.56	87.7	2.33	34.46	8.18	
						4.400	26.00	6.23	83.4	2.37	34.69	8.21	
						4.400	26.00	6.25	83.7	2.47	34.69	8.25	
2013/5/10 9:12	WY2	MF	829006	810395	9.8	1.000	26.20	5.97	79.8	2.07	34.27	8.02	1.9
						1.000	26.20	5.96	79.8	1.83	34.45	8.04	
						4.900	26.00	5.79	77.3	1.95	34.64	8.04	
						4.900	26.00	5.82	77.9	2.10	34.68	7.97	
2013/5/10 9:00	WY3	MF	829006	810395	5.7	8.800	25.90	5.80	77.5	1.93	34.67	8.18	6.4
						8.800	25.90	6.02	80.2	1.97	34.61	8.09	
						1.000	26.20	6.24	83.7	2.43	34.59	8.14	
						1.000	26.20	6.36	85.3	2.47	34.59	8.19	
2013/5/10 9:26	CY1	MF	828421	810817	13.7	4.700	26.00	6.45	86.4	2.52	34.71	8.38	5.1
						4.700	26.00	6.29	84.3	2.55	34.70	8.39	
						1.000	26.40	6.41	85.4	1.87	34.55	8.13	
						1.000	26.40	6.40	85.2	1.92	34.55	8.14	
2013/5/10 8:37	CY2	MF	828023	808814	17.3	6.850	26.20	6.30	83.4	1.83	33.82	8.19	3.2
						6.850	26.20	6.30	83.7	1.86	34.53	8.22	
						12.700	25.90	5.28	70.2	1.87	34.70	8.27	
						12.700	25.90	5.28	70.1	1.73	34.70	8.25	
2013/5/10 8:37	CY2	MF	828023	808814	17.3	1.000	26.30	8.35	109.4	1.96	32.50	8.45	4.1
						1.000	26.30	8.19	108.9	2.11	34.30	8.47	
						8.650	26.00	8.05	106.8	1.83	34.74	8.53	
						8.650	26.00	8.05	106.9	1.97	34.72	8.55	
2013/5/10 8:37	CY2	MF	828023	808814	17.3	16.300	25.70	7.53	100.2	1.92	34.73	8.60	11
						16.300	25.70	8.14	108.3	1.98	34.70	8.63	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 14-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/14 13:47	WY1	ME	829166	809557	4.2	1.000	26.60	8.48	111.6	1.46	31.40	7.70	2.8
						1.000	26.60	8.25	110.0	1.49	34.06	7.69	
						3.200	26.30	7.99	106.3	1.54	34.39	7.64	
						3.200	26.30	7.96	105.9	1.61	34.45	7.65	
2013/5/14 14:08	WY2	ME	829011	810416	8.4	1.000	26.60	7.75	102.5	1.52	33.78	7.68	1.2
						1.000	26.60	7.73	102.0	1.60	33.36	7.68	
						4.200	26.30	8.19	102.9	1.55	26.45	7.64	
						4.200	26.30	8.03	102.5	1.58	28.81	7.65	
						7.400	26.10	8.21	103.2	1.42	26.90	7.62	
						7.400	26.10	7.92	102.3	1.47	30.88	7.63	
2013/5/14 13:56	WY3	ME	829218	809836	4.4	1.000	26.60	7.57	99.3	1.51	31.49	7.62	4.3
						1.000	26.60	7.35	97.8	1.55	33.50	7.61	
						3.400	26.30	7.65	101.6	1.59	34.31	7.62	
						3.400	26.30	7.57	100.6	1.67	34.30	7.61	
2013/5/14 14:21	CY1	ME	828419	810823	12.2	1.000	26.70	8.03	99.2	1.37	24.28	7.68	1.6
						1.000	26.70	8.00	98.8	1.36	24.19	7.68	
						6.100	26.10	7.75	102.0	1.48	33.83	7.66	
						6.100	26.10	7.83	101.8	1.44	31.92	7.66	
						11.200	25.70	8.21	102.4	1.29	26.62	7.67	
11.200	25.70	7.83	102.6	1.20	33.57	7.67							
2013/5/14 14:39	CY2	ME	828025	808813	16.2	1.000	26.70	8.46	110.3	1.24	29.75	7.67	1
						1.000	26.70	8.20	109.8	1.33	33.20	7.67	
						8.100	25.90	8.68	109.9	1.36	27.79	7.57	
						8.100	25.90	8.81	109.8	1.41	25.62	7.57	
						15.200	25.50	8.26	109.2	1.23	34.06	7.55	
						15.200	25.50	8.09	107.6	1.25	34.75	7.55	
2013/5/14 9:06	WY1	MF	829176	809543	5.1	1.000	25.60	8.14	103.8	1.20	25.51	7.72	3
						1.000	25.60	8.05	102.6	1.30	25.36	7.70	
						4.100	25.40	7.52	100.5	1.31	33.63	7.65	
						4.100	25.40	7.58	100.6	1.47	32.64	7.65	
2013/5/14 8:46	WY2	MF	829011	810406	9.2	1.000	25.60	7.73	102.6	1.16	34.17	7.71	1.1
						1.000	25.60	7.63	101.5	1.28	34.19	7.65	
						4.600	25.40	7.91	99.8	1.23	27.08	7.58	
						4.600	25.40	7.98	99.7	1.32	25.65	7.58	
						8.200	25.20	7.62	99.2	1.19	32.22	7.56	
						8.200	25.20	7.54	98.6	1.26	32.77	7.56	
2013/5/14 8:57	WY3	MF	829195	809857	5.3	1.000	25.60	7.55	101.6	1.17	33.98	7.69	2.4
						1.000	25.60	7.53	101.4	1.33	34.10	7.68	
						4.300	25.40	7.38	99.3	1.35	34.60	7.63	
						4.300	25.40	7.32	98.5	1.28	34.60	7.62	
2013/5/14 8:31	CY1	MF	828413	810811	13.3	1.000	25.80	7.36	97.5	1.04	33.76	7.52	3.4
						1.000	25.80	7.34	97.1	1.08	33.74	7.52	
						6.650	25.40	7.41	98.2	1.16	34.62	7.51	
						6.650	25.40	7.42	98.5	1.22	34.63	7.51	
						12.300	25.10	7.29	96.5	1.11	34.77	7.51	
						12.300	25.10	7.34	97.2	1.05	34.77	7.51	
2013/5/14 9:22	CY2	MF	828012	808823	17.1	1.000	25.70	7.25	97.2	1.09	34.58	7.48	1.5
						1.000	25.70	7.26	97.4	1.01	34.59	7.47	
						8.550	25.30	7.59	96.0	1.13	26.53	7.50	
						8.550	25.30	7.86	96.0	1.19	20.55	7.51	
						16.100	24.90	6.81	90.0	0.97	34.66	7.51	
						16.100	24.90	6.80	89.7	1.04	34.69	7.51	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 16-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l	
			East	North										
2003/5/16 15:11	WY1	ME	829180	809543	4.3	1.000	26.10	7.43	99.8	2.47	34.90	7.77	5.2	
						1.000	26.10	7.37	98.7	2.52	34.54	7.74		
						3.300	25.80	7.21	96.4	2.79	35.13	7.67		
						3.300	25.80	7.33	98.0	2.83	35.08	7.66		
2013/5/16 15:32	WY2	ME	829008	810411	7.9	1.000	26.10	8.49	113.4	1.94	34.86	7.77	5.7	
						1.000	26.10	8.42	112.9	2.03	34.87	7.76		
						3.950	25.70	8.32	111.2	1.97	35.12	7.72	6.3	
						3.950	25.70	8.31	110.9	1.86	35.04	7.71		
						6.900	25.30	8.11	107.8	1.92	35.92	7.67		
2013/5/16 15:20	WY3	ME	829206	809847	4.5	1.000	25.30	8.15	108.4	1.99	35.96	7.65	7	
						1.000	26.10	8.21	110.2	2.22	34.89	7.83		
						1.000	26.10	7.97	107.0	2.28	34.91	7.80		
						3.500	25.80	7.60	101.7	2.74	35.15	7.73		
2013/5/16 15:46	CY1	ME	828406	810823	12.1	1.000	25.90	8.36	111.6	1.88	34.74	7.85	4	
						1.000	25.90	8.39	111.9	1.81	34.73	7.82		
						6.050	25.60	8.40	111.6	1.74	35.17	7.73	3.7	
						6.050	25.60	8.30	110.2	1.87	35.06	7.71		
						11.100	24.90	8.10	107.4	1.77	35.77	7.69		
2013/5/16 16:05	CY2	ME	827984	808812	16.3	1.000	24.90	8.07	107.0	1.66	35.80	7.67	8.5	
						1.000	25.90	7.71	102.8	1.74	34.68	7.80		
						1.000	25.90	7.77	103.7	1.75	34.68	7.77	7.4	
						8.150	25.20	7.82	103.7	1.63	35.63	7.74		
						8.150	25.20	7.78	103.1	1.59	35.63	7.73		
2013/5/16 16:05	CY2	ME	827984	808812	16.3	15.300	24.40	7.89	104.7	1.42	36.00	7.70	8.7	
						15.300	24.40	7.75	102.6	1.60	35.96	7.70		
						1.000	25.00	8.04	107.5	2.04	34.60	7.98		9
						1.000	25.00	7.93	106.0	2.18	34.63	7.91		
2013/5/16 9:10	WY1	MF	829154	809551	5.5	4.500	24.60	8.20	109.3	2.17	34.87	7.79	7.7	
						4.500	24.60	8.13	108.4	2.27	34.85	7.77		
						1.000	25.00	8.11	109.4	1.82	34.76	7.86		
						1.000	25.00	8.02	108.1	1.94	34.75	7.84		
2013/5/16 8:50	WY2	MF	829014	810425	9.7	4.850	24.70	8.07	108.4	1.82	35.12	7.77	7.8	
						4.850	24.70	7.92	106.3	1.86	35.18	7.77		
						8.700	24.30	8.37	111.4	1.75	35.59	7.71	11.2	
						8.700	24.30	8.07	107.3	1.83	35.62	7.70		
						1.000	25.00	8.28	111.3	1.94	34.84	7.81		
2013/5/16 9:01	WY3	MF	829201	809833	5.8	1.000	25.00	8.03	107.9	2.03	34.83	7.80	4.5	
						4.800	24.60	7.93	105.9	2.15	35.05	7.74		
						4.800	24.60	7.93	105.7	2.12	34.86	7.74	7.2	
						1.000	25.20	8.12	108.0	1.69	34.27	7.75		
2013/5/16 8:37	CY1	MF	828407	810779	13.4	1.000	25.20	8.23	109.5	1.74	34.30	7.73	6.6	
						6.700	24.60	8.23	109.6	1.72	35.21	7.68		
						6.700	24.60	8.07	107.5	1.63	35.26	7.68	5.6	
						12.400	24.10	8.45	112.0	1.58	35.83	7.63		
						12.400	24.10	8.39	111.3	1.66	35.85	7.61		
2013/5/16 9:27	CY2	MF	828013	808816	17.6	1.000	25.30	8.20	110.7	1.53	35.28	7.93	6.2	
						1.000	25.30	8.17	110.3	1.61	35.33	7.91		
						8.800	24.50	8.37	111.0	1.48	36.04	7.79	7.3	
						8.800	24.50	8.36	110.9	1.49	36.04	7.77		
						16.600	23.90	8.12	107.6	1.41	35.71	7.69		
2013/5/16 9:27	CY2	MF	828013	808816	17.6	16.600	23.90	8.09	107.1	1.47	35.70	7.69	8.7	
						16.600	23.90	8.09	107.1	1.47	35.70	7.69		

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 18-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/18 16:53	WY1	ME	829183	809559	4.2	1.000	26.20	7.58	100.9	3.06	33.79	7.77	2.7
						1.000	26.20	7.87	104.8	6.14	33.84	7.74	
						3.200	25.90	8.06	107.2	6.17	34.18	7.70	
						3.200	25.90	8.11	107.8	6.19	34.19	7.68	
2013/5/16 17:13	WY2	ME	829017	810422	7.7	1.000	26.20	7.63	101.6	2.84	34.02	7.62	2.9
						1.000	26.20	8.06	107.2	2.72	34.03	7.59	
						3.850	25.80	8.30	110.3	2.79	34.02	7.60	
						3.850	25.80	8.30	110.2	2.88	34.01	7.60	
						6.700	25.40	8.38	110.9	2.67	34.48	7.56	
						6.700	25.40	8.35	110.6	2.73	34.61	7.59	
2013/5/16 17:02	WY3	ME	829194	809831	4.4	1.000	26.20	7.52	100.3	2.98	33.97	7.73	2.4
						1.000	26.20	7.81	104.3	3.11	33.98	7.70	
						3.400	25.90	8.28	110.2	3.26	34.24	7.68	
						3.400	25.90	8.38	111.6	3.16	34.23	7.66	
2013/5/16 17:27	CY1	ME	828377	810786	12.4	1.000	26.30	8.19	108.0	2.37	33.05	7.48	4.5
						1.000	26.30	8.35	110.0	2.45	32.97	7.46	
						6.200	25.50	8.33	109.2	2.19	33.59	7.46	
						6.200	25.50	8.42	110.5	2.31	33.68	7.46	
						11.400	24.90	8.27	109.3	2.11	35.08	7.44	
						11.400	24.90	8.39	110.5	2.06	34.31	7.44	
2013/5/16 17:46	CY2	ME	828029	808808	15.9	1.000	26.40	7.70	102.3	2.26	33.88	7.68	3.6
						1.000	26.40	7.64	101.7	2.26	34.03	7.67	
						7.950	25.40	7.75	103.0	2.03	34.79	7.64	
						7.950	25.40	7.71	102.4	2.14	34.80	7.62	
						14.900	24.80	7.58	100.5	1.96	35.14	7.61	
						14.900	24.80	7.62	100.3	2.07	34.06	7.58	
2013/5/16 11:00	WY1	MF	829176	809531	5.1	1.000	25.40	7.80	103.2	2.31	32.90	7.59	1.8
						1.000	25.40	7.87	104.1	2.26	32.87	7.56	
						4.100	25.00	8.21	107.8	2.39	33.85	7.53	
						4.100	25.00	8.14	106.8	2.44	33.88	7.50	
2013/5/16 10:40	WY2	MF	829003	810388	8.9	1.000	25.30	8.84	117.8	2.06	33.94	7.45	2.5
						1.000	25.30	8.74	116.5	1.99	33.95	7.43	
						4.450	25.00	8.89	117.7	2.12	35.05	7.38	
						4.450	25.00	8.83	116.9	2.20	35.03	7.34	
						7.900	24.60	8.71	115.2	1.93	35.06	7.29	
						7.900	24.60	8.66	114.5	1.97	35.06	7.28	
2013/5/16 10:51	WY3	MF	829196	809855	5.3	1.000	25.40	7.62	101.3	2.18	34.00	7.57	2.4
						1.000	25.40	7.72	102.8	2.24	33.98	7.56	
						4.300	25.00	7.75	102.3	2.32	34.86	7.52	
						4.300	25.00	7.82	103.2	2.37	34.92	7.50	
2013/5/16 10:27	CY1	MF	828387	810781	13.3	1.000	25.10	8.69	115.9	1.83	33.87	7.13	4.7
						1.000	25.10	8.74	116.2	1.87	33.85	7.10	
						6.650	24.80	8.85	116.6	1.86	34.50	7.04	
						6.650	24.80	8.81	116.3	1.92	34.99	7.00	
						12.300	24.30	8.57	112.8	1.76	34.53	6.95	
						12.300	24.30	8.54	112.7	1.88	35.09	6.91	
2013/5/16 11:16	CY2	MF	828012	808783	16.8	1.000	25.00	8.27	109.2	1.81	33.30	7.42	1.3
						1.000	25.00	8.14	107.8	1.72	33.99	7.41	
						8.400	24.40	7.93	104.6	1.87	35.21	7.34	
						8.400	24.40	7.92	104.5	1.83	35.23	7.34	
						15.800	23.90	7.34	95.8	1.62	34.63	7.37	
						15.800	23.90	7.28	95.6	1.79	35.39	7.37	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 20-May-13

Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/20 8:51	WY1	ME	829179	809546	4.5	1.000	24.90	8.96	118.7	3.03	35.41	7.86	5.2
						1.000	24.90	9.17	120.9	2.97	34.67	7.83	
						3.500	24.40	7.27	96.4	3.06	35.48	7.78	
						3.500	24.40	7.31	96.9	3.18	35.49	7.76	
2013/5/20 9:11	WY2	ME	828988	810410	8.3	1.000	24.80	8.62	114.5	3.02	35.32	7.72	3.2
						1.000	24.80	8.86	117.5	2.83	35.34	7.72	
						4.150	24.30	7.99	106.0	2.75	35.45	7.73	6.7
						4.150	24.30	7.85	104.1	2.89	35.46	7.73	
						7.300	23.90	7.40	98.0	2.71	35.36	7.70	6.9
						7.300	23.90	7.47	98.4	2.77	34.46	7.72	
2013/5/20 9:00	WY3	ME	829207	809861	4.8	1.000	24.90	8.55	113.6	3.08	35.41	7.69	7.2
						1.000	24.90	8.61	114.4	3.12	35.32	7.68	
						3.800	24.40	7.35	96.8	3.14	34.42	7.69	
						3.800	24.40	7.28	96.5	3.22	35.51	7.68	
2013/5/20 9:25	CY1	ME	828421	810813	12.7	1.000	25.00	7.29	97.8	2.81	35.24	7.66	2.4
						1.000	25.00	8.40	112.3	2.80	35.27	7.68	
						6.350	24.20	7.75	102.8	2.62	35.34	7.70	5.2
						6.350	24.20	7.87	104.4	2.66	35.35	7.67	
						11.700	23.60	7.42	98.6	2.57	35.42	7.71	6.4
						11.700	23.60	7.42	98.4	2.69	35.42	7.72	
2013/5/20 9:42	CY2	ME	828012	808817	15.9	1.000	25.00	8.37	111.4	2.73	34.00	7.95	3.3
						1.000	25.00	8.34	110.6	2.74	33.55	7.93	
						7.950	24.10	8.54	113.4	2.67	35.11	7.88	6.9
						7.950	24.10	8.63	114.7	2.70	35.52	7.88	
						14.900	23.40	8.71	115.9	2.49	35.59	7.87	7.6
						14.900	23.40	8.67	115.4	2.43	35.64	7.87	
2013/5/20 13:33	WY1	MF	829165	809558	5.6	1.000	25.70	8.74	116.3	2.51	35.40	7.96	5.1
						1.000	25.70	9.47	125.8	2.65	35.45	7.94	
						4.600	25.20	7.46	99.2	2.59	35.86	7.92	
						4.600	25.20	7.42	98.7	2.67	35.91	7.92	
2013/5/20 13:54	WY2	MF	829019	810403	9.8	1.000	25.60	9.13	121.0	2.44	35.38	7.93	5.2
						1.000	25.60	9.33	123.6	2.51	35.38	7.89	
						4.900	25.10	7.87	104.2	2.41	35.50	7.89	6.2
						4.900	25.10	7.94	104.5	2.46	34.55	7.89	
						8.800	24.80	7.46	98.2	2.32	34.25	7.89	7.1
						8.800	24.80	7.35	97.8	2.47	35.85	7.90	
2013/5/20 13:42	WY3	MF	829184	809843	5.9	1.000	25.70	9.19	121.8	2.43	35.46	7.95	4.5
						1.000	25.70	9.46	125.5	2.60	35.45	7.92	
						4.900	25.20	7.29	96.8	2.72	35.74	7.92	
						4.900	25.20	7.47	99.0	2.75	35.20	7.90	
2013/5/20 14:07	CY1	MF	828414	808783	13.8	1.000	25.80	8.97	118.7	2.16	35.30	7.92	4.6
						1.000	25.80	9.13	120.8	2.25	35.31	7.91	
						6.900	25.00	7.74	102.6	2.23	35.24	7.89	4.2
						6.900	25.00	7.72	102.4	2.29	35.21	7.88	
						12.800	24.60	7.18	95.3	2.08	35.80	7.89	12.7
						12.800	24.60	7.21	95.9	2.11	35.81	7.90	
2013/5/20 14:23	CY2	MF	828025	808816	18	1.000	25.80	8.80	116.5	2.07	35.51	7.95	6.5
						1.000	25.80	8.97	118.8	2.18	35.51	7.93	
						9.000	25.00	7.61	100.5	2.14	35.20	7.89	6.5
						9.000	25.00	7.68	101.0	2.26	34.64	7.90	
						17.000	24.40	7.05	93.4	1.98	35.76	7.89	6.5
						17.000	24.40	7.09	93.8	2.09	35.16	7.87	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide

Marine Water Quality Monitoring Result at Yung Shue Wan

Date 24-May-13



Date / Time	Location	Tide*	Co-ordinates		Water Depth m	Sampling Depth m	Temp °C	DO Conc mg/L	DO Saturation %	Turbidity NTU	Salinity ppt	pH unit	SS mg/l
			East	North									
2013/5/24 11:34	WY1	ME	829173	809567	4.4	1.000	27.10	7.40	98.8	3.45	34.74	7.81	2.4
						1.000	27.10	7.52	100.8	3.56	35.30	7.79	
						3.400	26.80	7.68	102.8	3.72	35.53	7.71	3
						3.400	26.80	7.74	103.3	3.79	35.06	7.69	
2013/5/24 11:54	WY2	ME	829021	810411	7.8	1.000	27.20	7.53	100.2	3.06	34.57	7.70	2.8
						1.000	27.20	7.68	102.8	3.17	35.34	7.69	
						3.900	26.80	7.74	103.1	3.08	35.57	7.66	4.5
						3.900	26.80	7.82	104.3	2.94	35.58	7.65	
						6.800	26.40	7.71	102.8	2.87	35.72	7.64	4.8
						6.800	26.40	7.64	101.8	3.03	35.73	7.64	
2013/5/24 11:43	WY3	ME	829218	809871	4.6	1.000	27.10	7.02	94.2	3.28	35.34	7.71	2.6
						1.000	27.10	7.38	99.1	3.41	35.38	7.69	
						3.600	26.80	7.77	104.0	3.59	35.56	7.63	5.9
						3.600	26.80	7.85	104.2	3.74	34.53	7.62	
2013/5/24 12:08	CY1	ME	828424	810827	12.1	1.000	27.10	7.15	95.9	2.83	34.87	7.70	2.9
						1.000	27.10	7.26	96.9	2.97	34.34	7.68	
						6.050	26.50	7.23	96.1	2.78	35.14	7.66	2.8
						6.050	26.50	7.46	99.2	2.91	35.16	7.65	
						11.100	26.10	7.39	98.7	2.73	35.44	7.64	3.4
						11.100	26.10	7.49	98.9	2.79	33.76	7.62	
2013/5/24 11:18	CY2	ME	828018	808822	15.6	1.000	27.00	7.18	96.0	2.97	35.11	7.63	1.9
						1.000	27.00	7.23	96.7	3.03	35.12	7.60	
						7.800	26.40	7.51	100.5	3.14	35.55	7.55	2.2
						7.800	26.40	7.56	101.1	3.26	35.59	7.54	
						14.600	26.00	7.37	98.2	2.82	35.44	7.52	2.1
						14.600	26.00	7.37	98.5	2.71	35.78	7.52	
2013/5/24 17:06	WY1	MF	829163	809558	5.4	1.000	27.60	7.36	97.5	2.26	34.12	7.73	7.4
						1.000	27.60	7.40	98.1	2.37	34.10	7.72	
						4.400	27.20	7.39	98.2	2.72	34.93	7.71	7.7
						4.400	27.20	7.41	98.4	2.66	34.90	7.68	
2013/5/24 17:27	WY2	MF	829013	810378	8.9	1.000	27.50	7.32	97.4	2.13	34.20	7.73	5.4
						1.000	27.50	7.33	97.9	2.35	34.84	7.71	
						4.450	27.10	7.38	98.4	2.21	34.86	7.66	5.3
						4.450	27.10	7.41	98.3	2.32	34.20	7.65	
						7.900	26.80	7.25	96.6	2.19	34.89	7.62	5.8
						7.900	26.80	7.26	96.8	2.08	34.91	7.63	
2013/5/24 17:15	WY3	MF	829204	809871	5.5	1.000	27.60	7.17	95.8	2.39	34.70	7.72	8.1
						1.000	27.60	7.17	95.7	2.47	34.74	7.70	
						4.500	27.20	7.43	98.9	2.61	34.87	7.65	9.8
						4.500	27.20	7.38	98.3	2.68	34.87	7.63	
2013/5/24 17:31	CY1	MF	828412	810820	13.4	1.000	27.90	7.06	94.5	1.96	35.07	7.65	2.2
						1.000	27.90	7.15	95.7	2.08	35.05	7.69	
						6.700	27.30	7.09	94.4	1.94	35.26	7.55	2.9
						6.700	27.30	7.05	94.0	1.97	35.28	7.59	
						12.400	26.70	6.99	93.2	2.03	35.52	7.55	3.3
						12.400	26.70	6.93	92.3	2.14	35.54	7.56	
2013/5/24 17:49	CY2	MF	828023	808825	17.2	1.000	27.90	6.44	86.5	1.87	35.04	7.26	6.7
						1.000	27.90	6.50	87.2	2.01	34.99	7.29	
						8.600	27.30	6.54	86.4	1.73	34.62	7.27	6.6
						8.600	27.30	6.53	86.6	1.88	35.39	7.24	
						16.200	26.60	6.37	84.8	1.82	35.57	7.28	7.3
						16.200	26.60	6.42	85.4	1.96	35.58	7.30	

Remarks: MF - Middle Flood tide
ME - Middle Ebb tide



Appendix H

Graphical Plots of Monitoring Results


1-hour TSP Monitoring

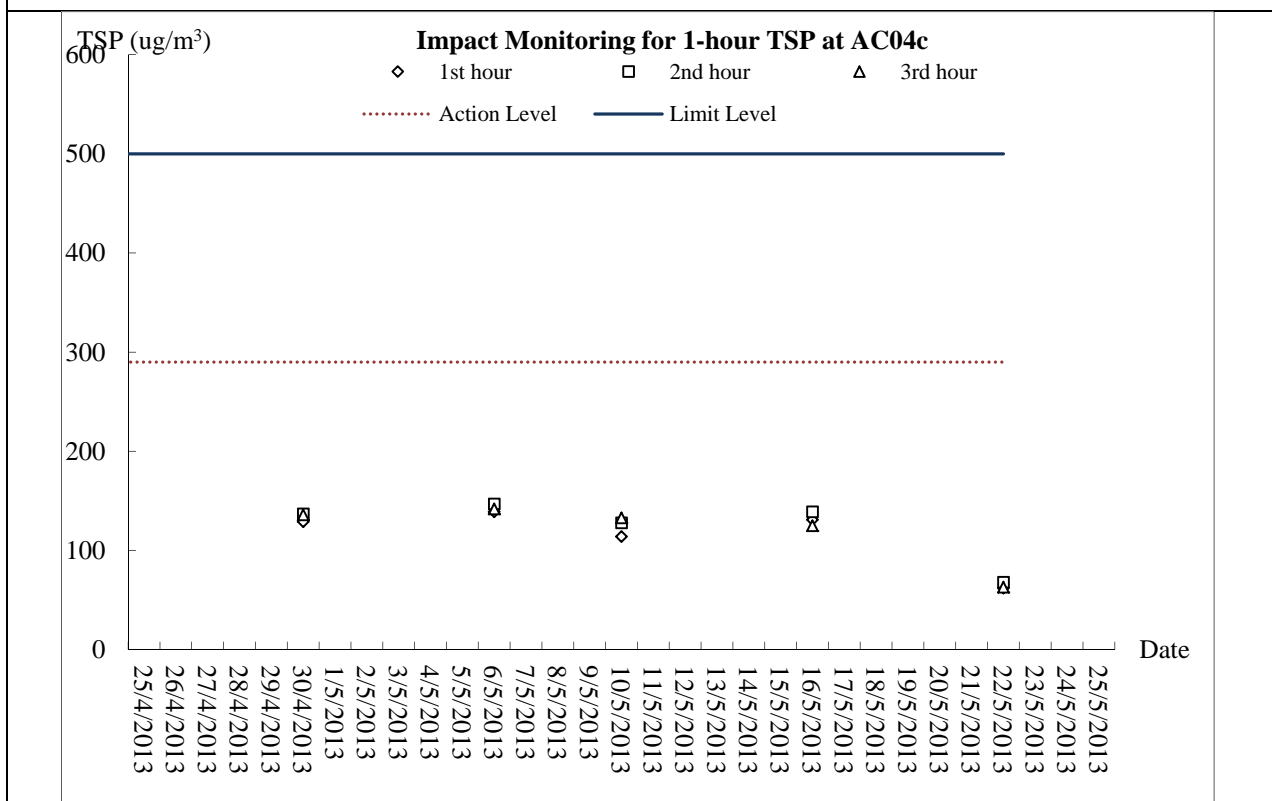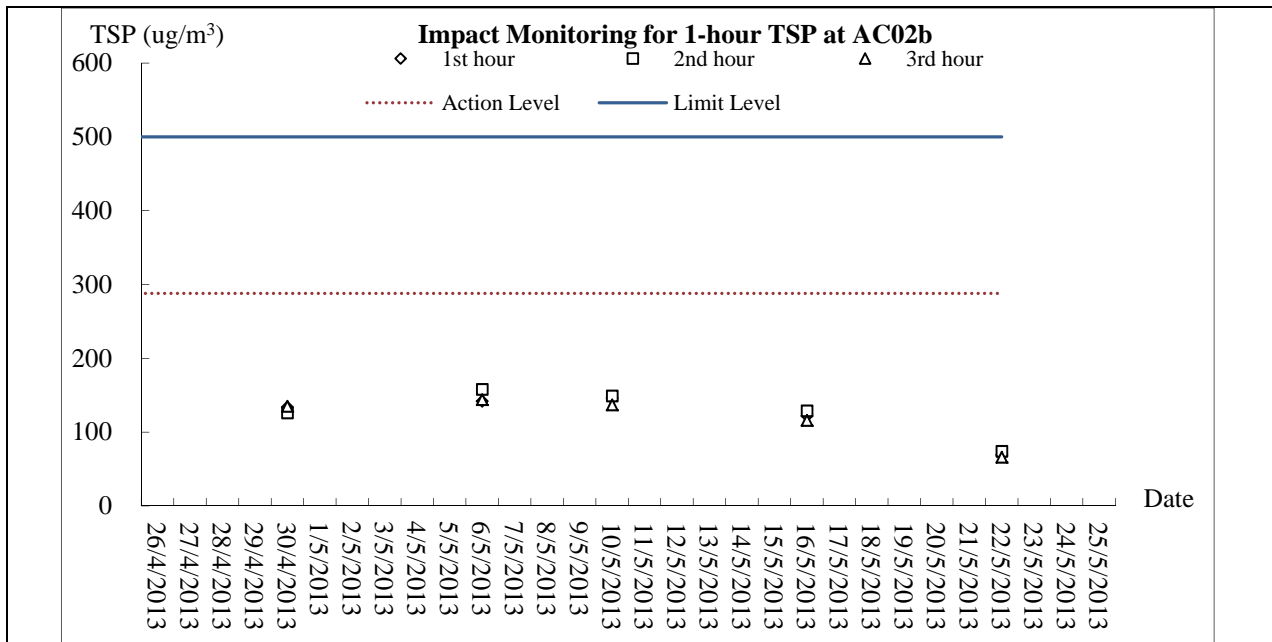



24-hour TSP Monitoring

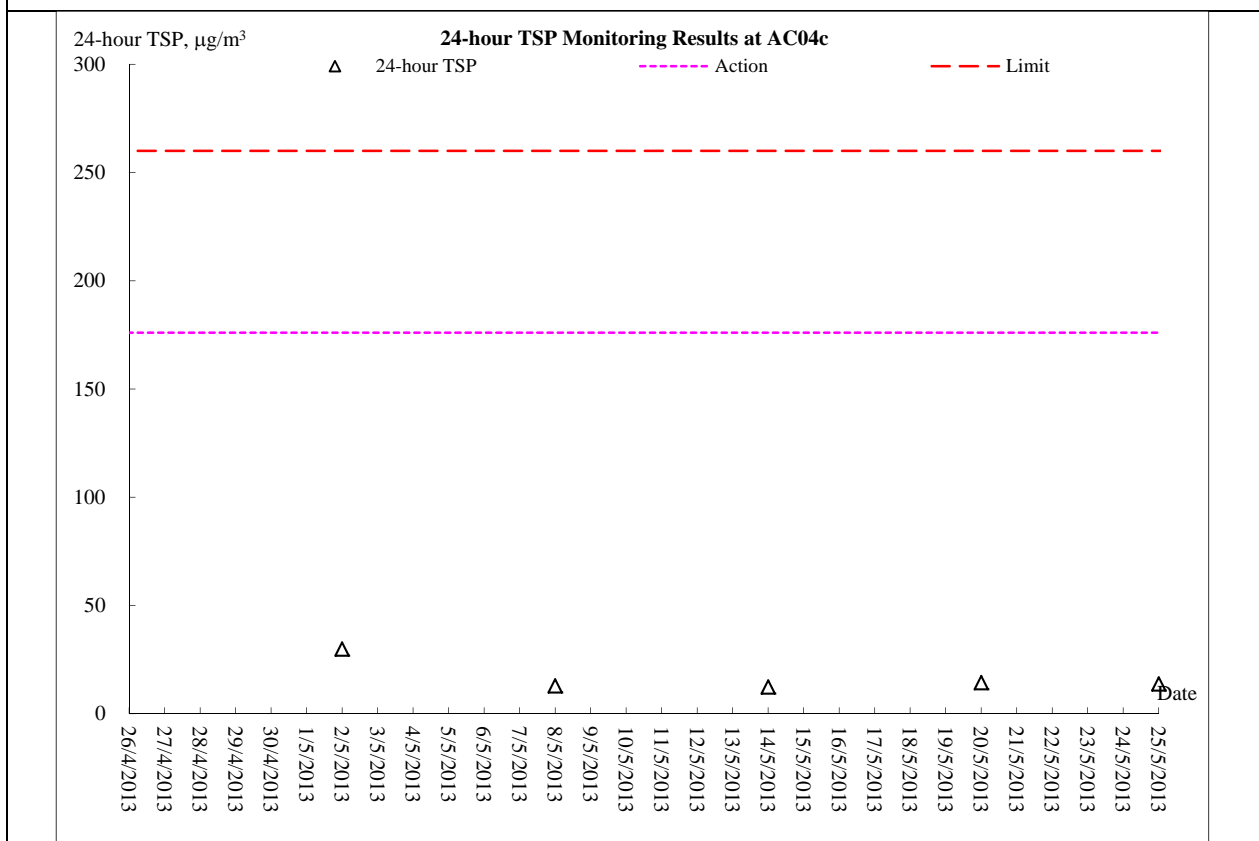
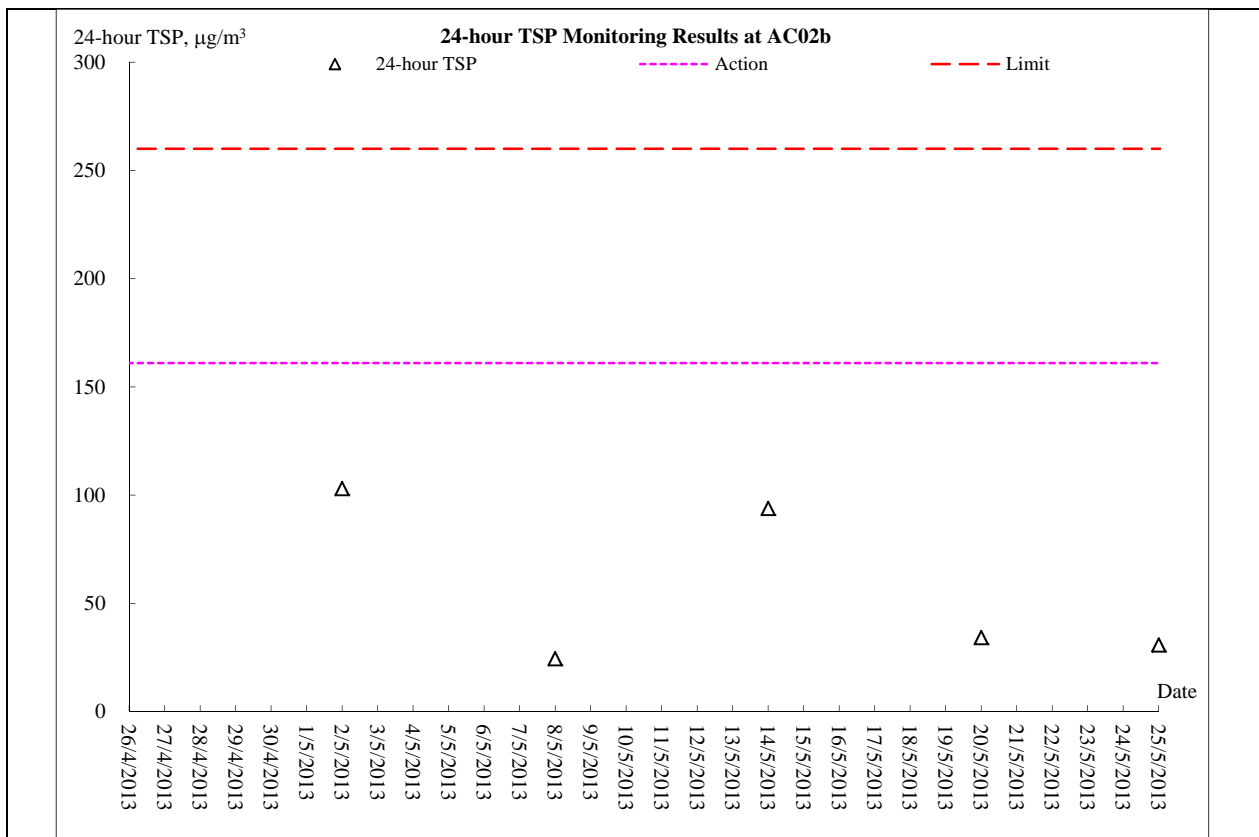


Noise Monitoring


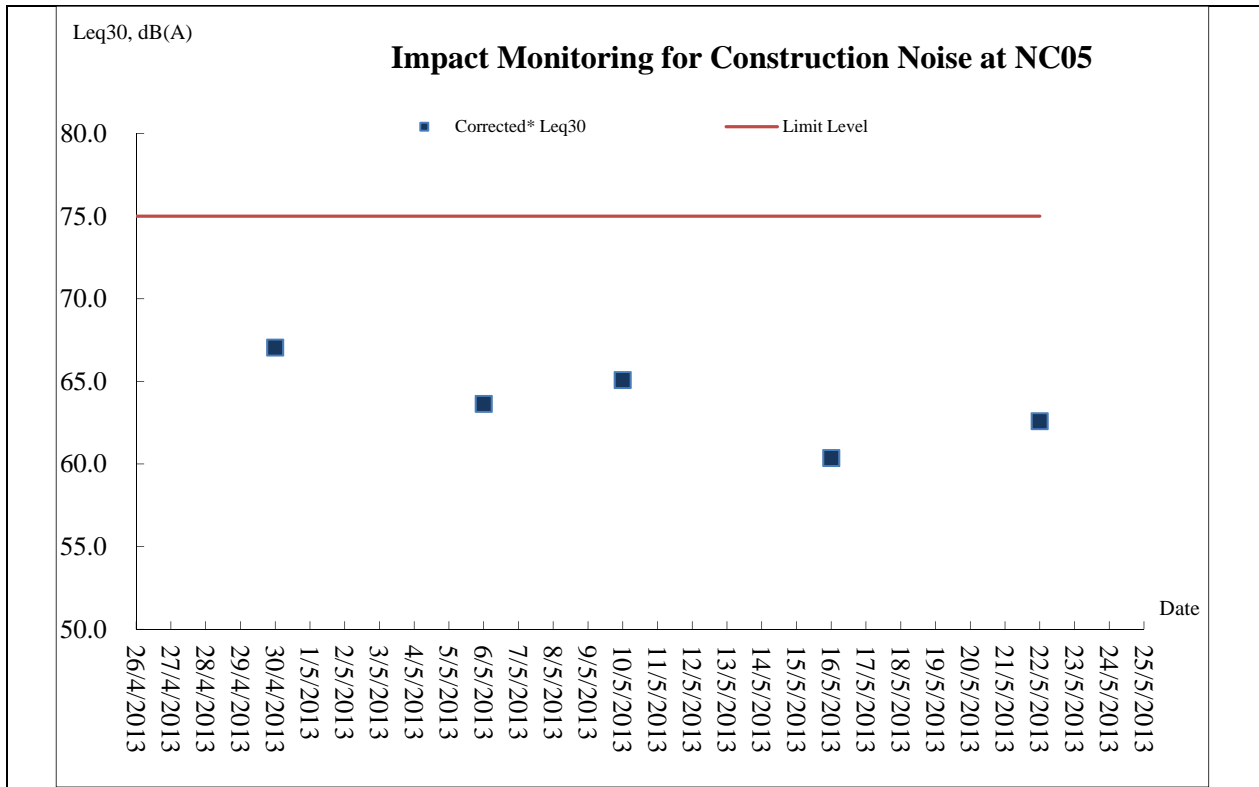




Marine Water Monitoring – Mid Ebb

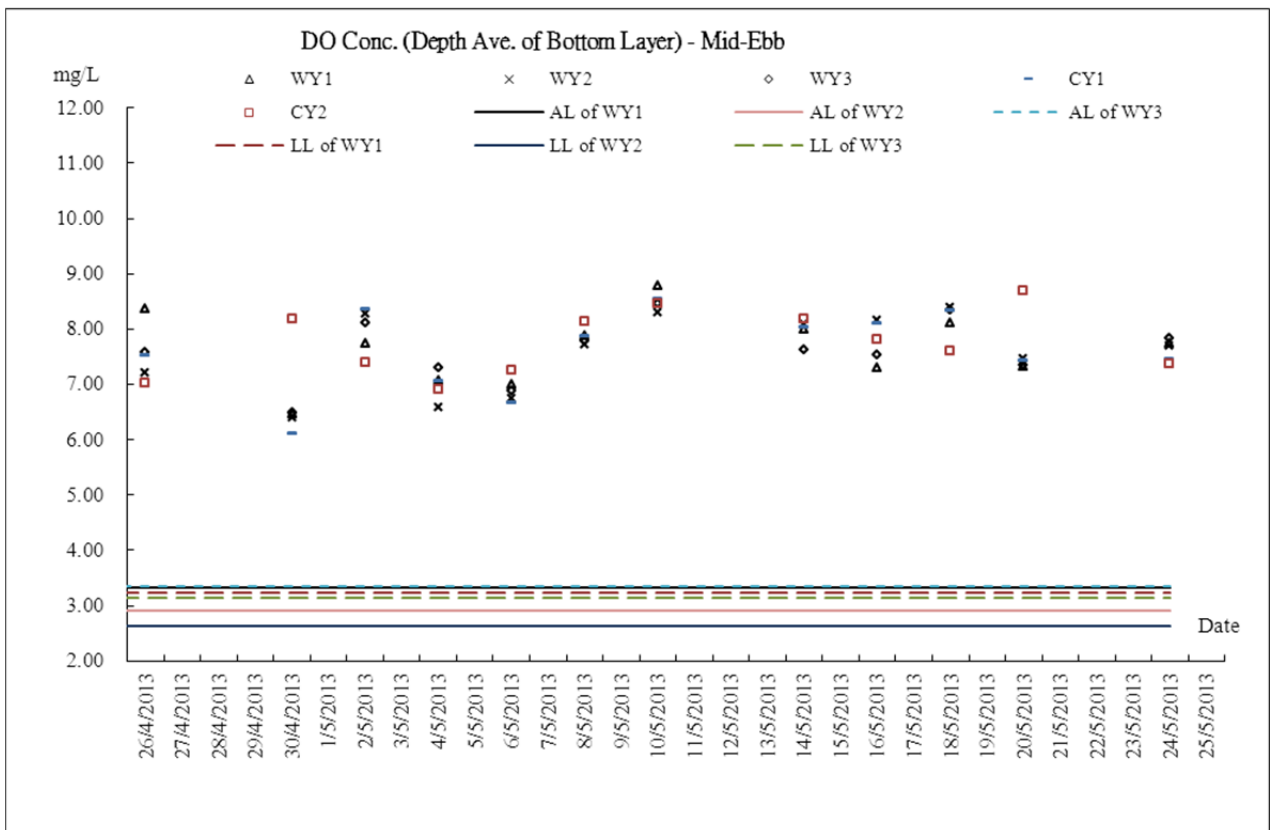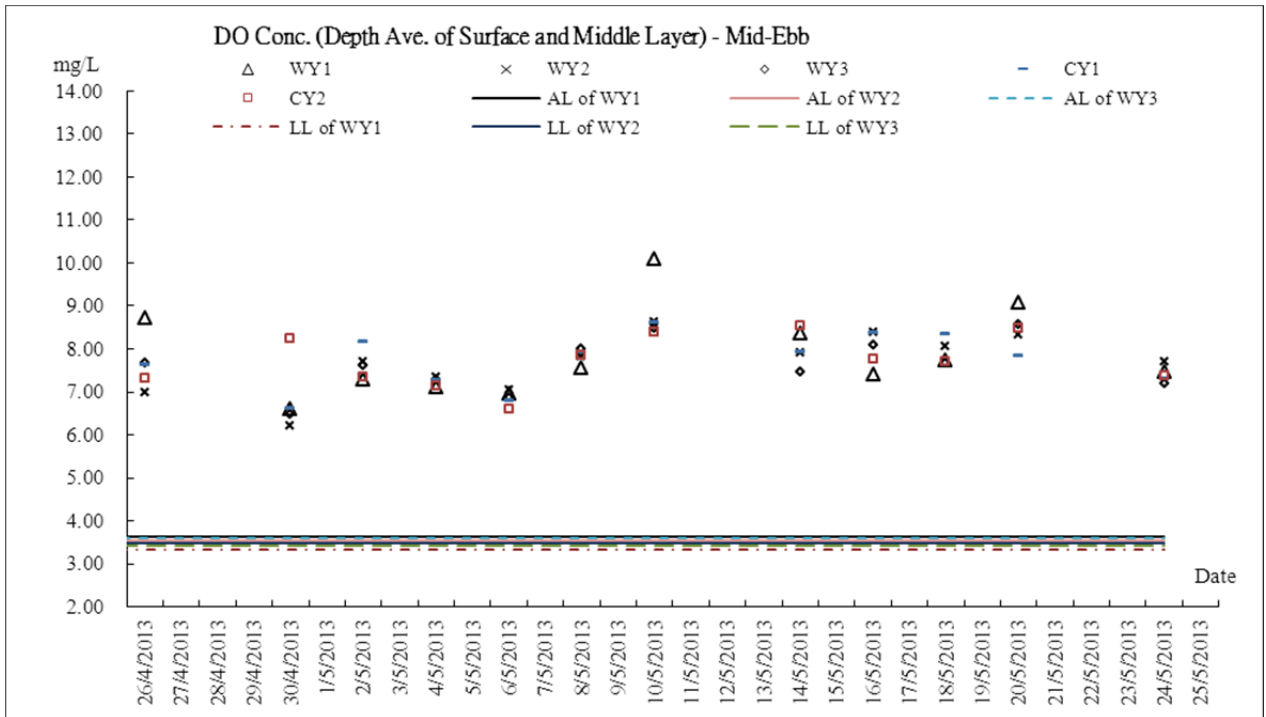

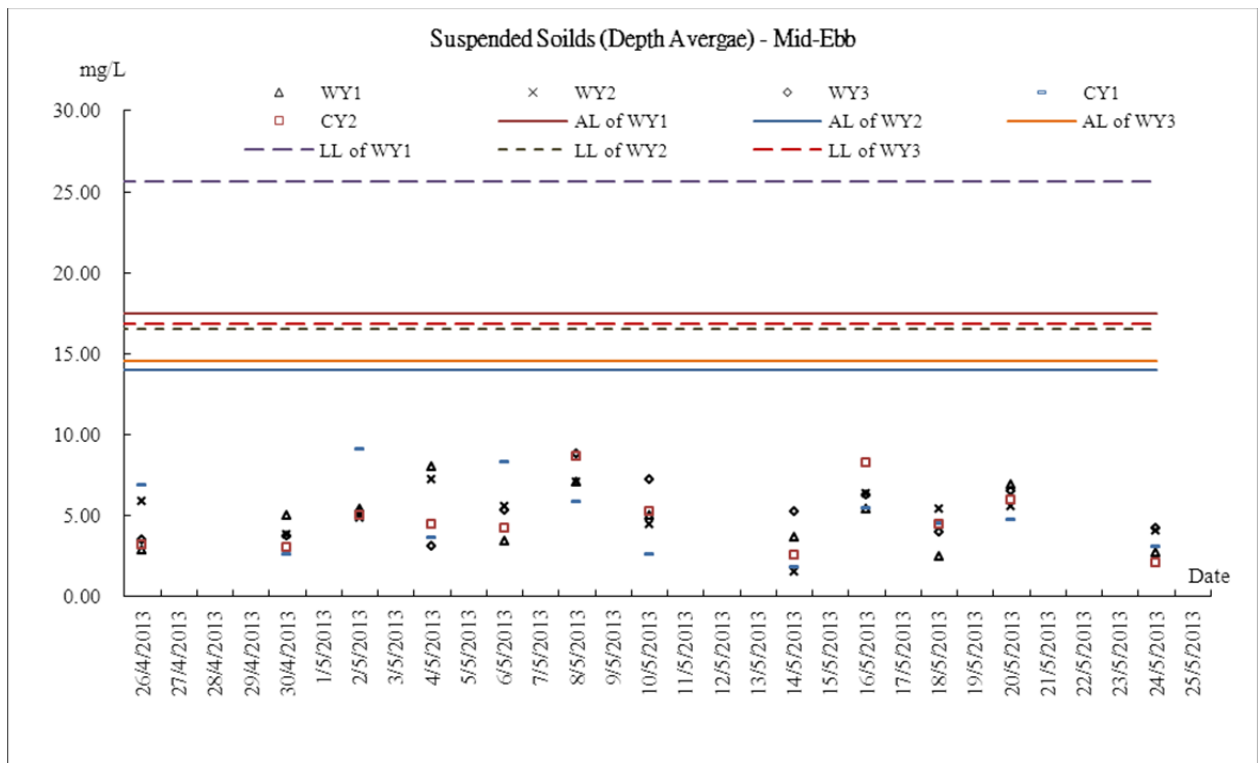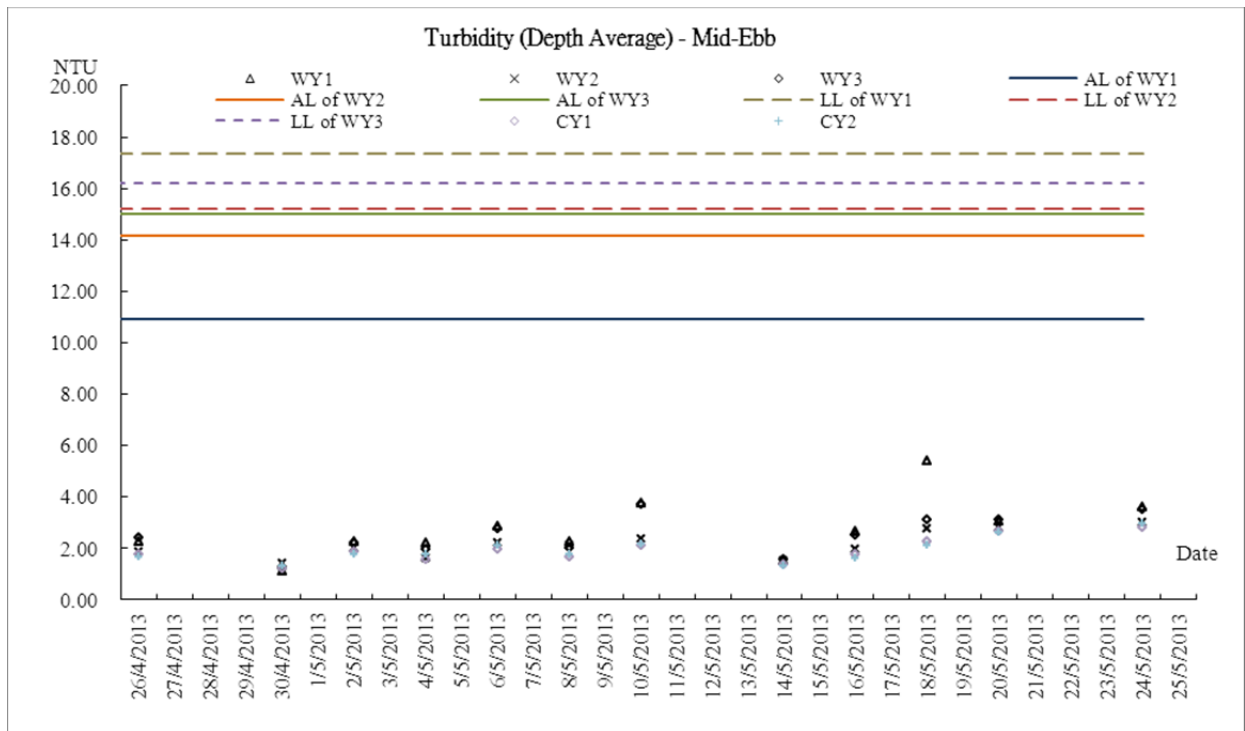

Marine Water Monitoring – Mid Flood

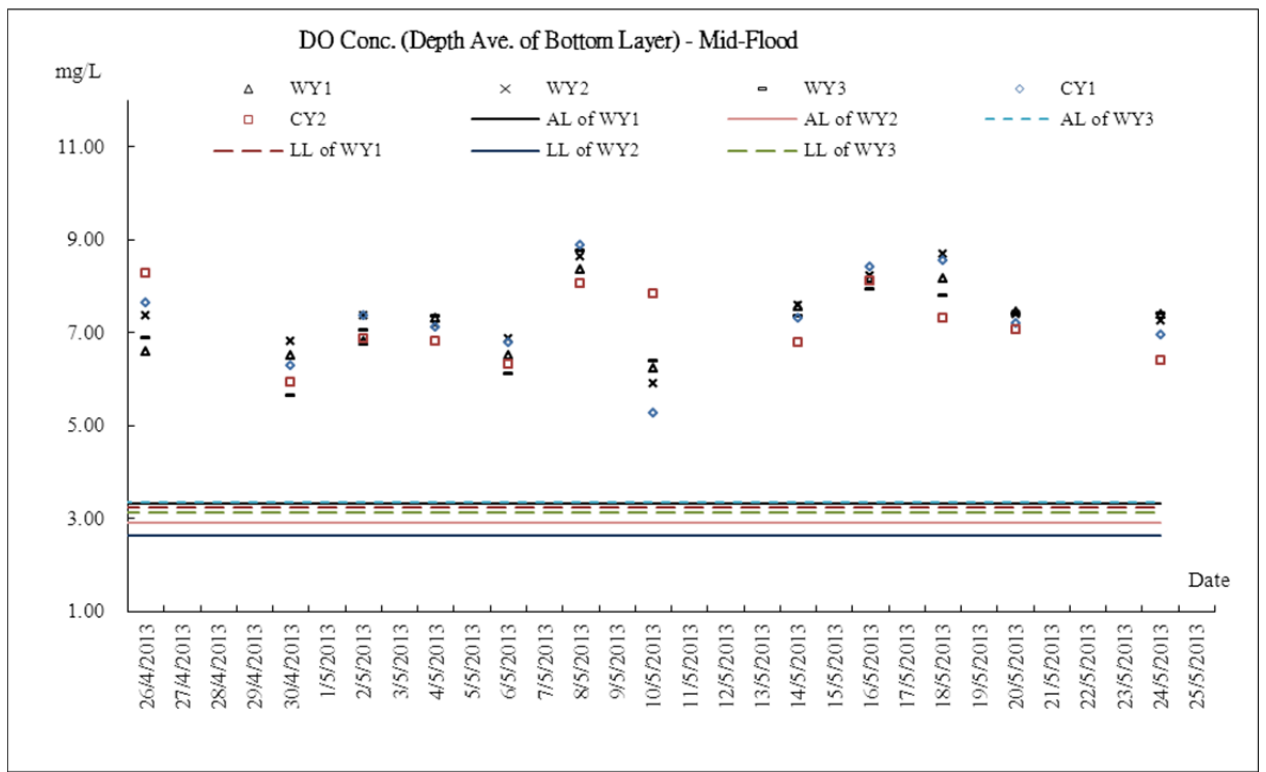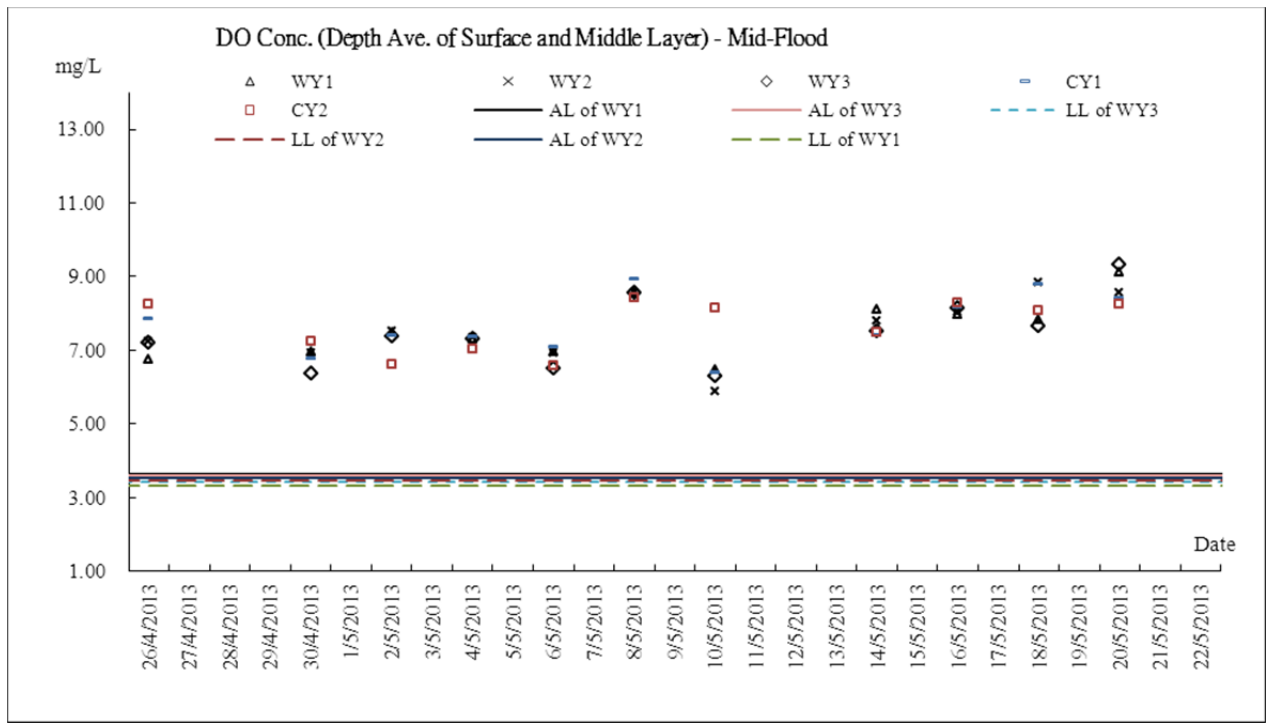

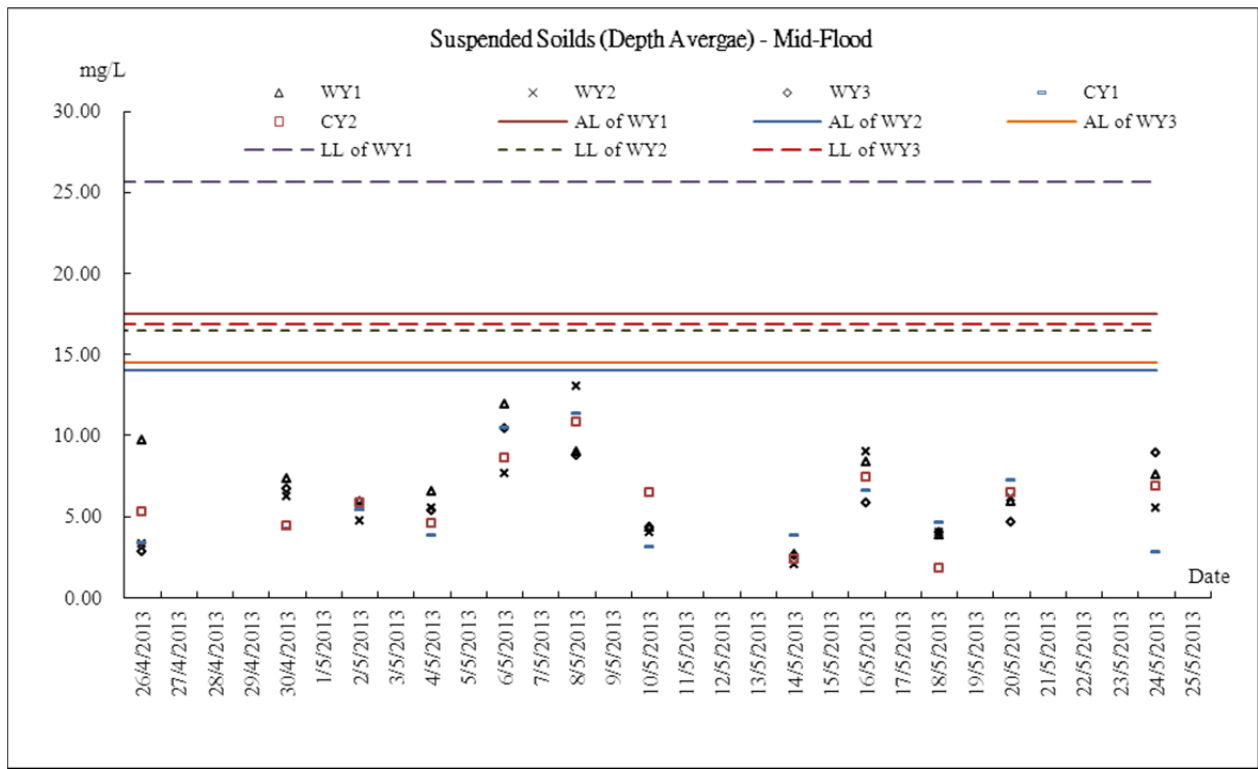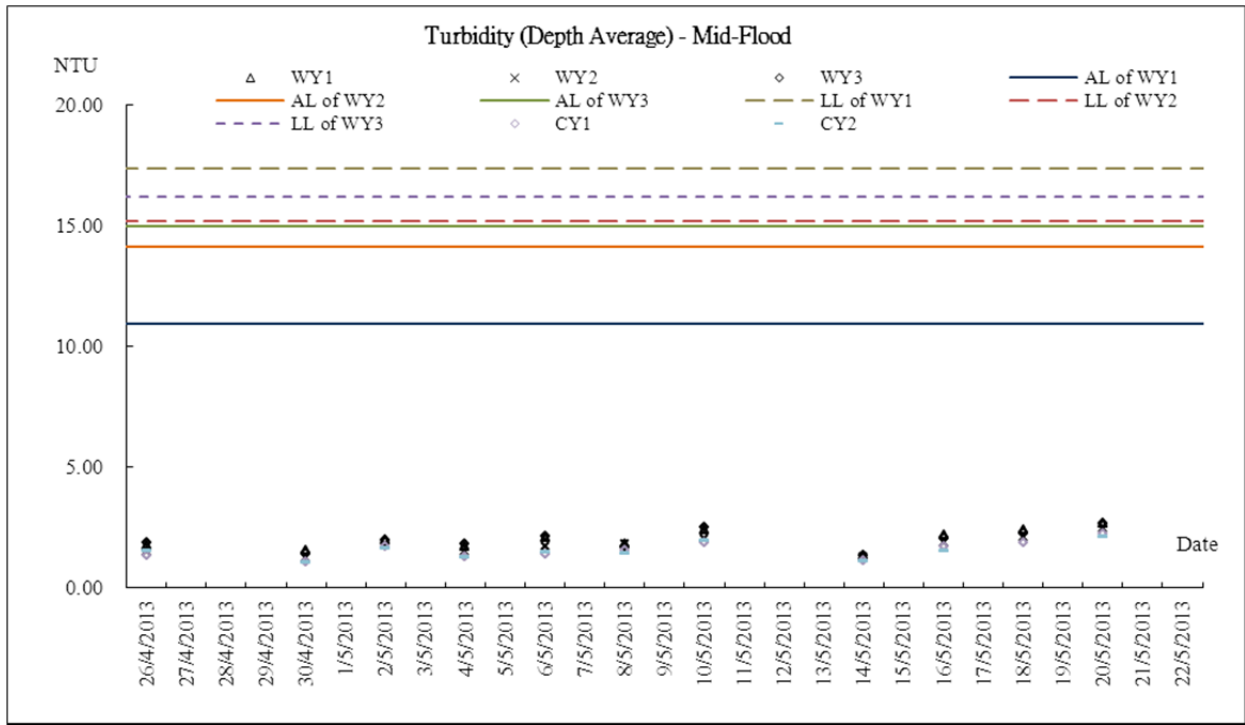

Appendix I

Meteorological Information

Meteorological Data Extracted from HKO during the Reporting Period

Date		Weather
26-Apr-13	Fri	Cloudy, rain, moderate to fresh easterly winds
27-Apr-13	Sat	Warm, sunny, moist.
28-Apr-13	Sun	Cloudy, rain, moderate to fresh easterly winds
29-Apr-13	Mon	Cloudy, fog, squally thunderstorms, light winds.
30-Apr-13	Tue	Cloudy, fog, squally thunderstorms, light winds.
1-May-13	Wed	Cloudy, rain, fresh easterly winds, strong offshore.
2-May-13	Thu	Cloudy, rain, fresh easterly winds, strong offshore.
3-May-13	Fri	Cloudy, rain, Moderate to fresh east to northeasterly winds.
4-May-13	Sat	Cloudy, rain, Moderate to fresh east to northeasterly winds.
5-May-13	Sun	Cloudy, mist, sunny intervals, moderate easterly winds.
6-May-13	Mon	Cloudy, mist, sunny intervals, moderate easterly winds.
7-May-13	Tue	Cloudy, mist, sunny intervals, moderate easterly winds.
8-May-13	Wed	Cloudy, rain, fog, moderate to fresh easterly winds.
9-May-13	Thu	Cloudy, a few showers, mist, showers, moderate southerly winds.
10-May-13	Fri	Cloudy, rain, fog, moderate to fresh easterly winds.
11-May-13	Sat	Cloudy, a few showers, mist, showers, moderate southerly winds.
12-May-13	Sun	Cloudy, sunny intervals, moderate east to southeasterly winds.
13-May-13	Mon	Cloudy, sunny intervals, isolated showers, mist, moderate east to southeasterly winds.
14-May-13	Tue	Cloudy, rain, squally thunderstorms, moderate south to southwesterly winds, fresh offshore.
15-May-13	Wed	Cloudy, sunny intervals, isolated showers, mist, moderate east to southeasterly winds.
16-May-13	Thu	Cloudy, rain, squally thunderstorms, moderate south to southwesterly winds, fresh offshore.
17-May-13	Fri	Cloudy, rain, fog, moderate to fresh easterly winds.
18-May-13	Sat	Cloudy, rain, squally thunderstorms, moderate south to southwesterly winds, fresh offshore.
19-May-13	Sun	Cloudy, rain, fog, moderate to fresh easterly winds.
20-May-13	Mon	Cloudy, rain, fog, moderate to fresh easterly winds.
21-May-13	Tue	Cloudy, rain, squally thunderstorms, moderate south to southwesterly winds, fresh offshore.
22-May-13	Wed	Cloudy, rain, squally thunderstorms, moderate south to southwesterly winds, fresh offshore.
23-May-13	Thu	Cloudy, rain, squally thunderstorms, moderate south to southwesterly winds, fresh offshore.
24-May-13	Fri	Cloudy, rain, squally thunderstorms, moderate south to southwesterly winds, fresh offshore.
25-May-13	Sat	Fine, very hot, light to moderate southerly winds.

Appendix J

Monthly Summary Waste Flow Table

Monthly Summary Waste Flow Table for December 2010

Month	Actual Quantities of Inert C&D Materials Generated Monthly												Actual Quantities of C&D Wastes Generated Monthly									
	Total Quantity Generated (a) = (c)+(d)+(e)		Hard Rock and Large Broken Concrete (b)		Reused in the Contract (c)		Reused in other Projects (d)		Disposed as Public Fill (e)		Imported Fill (f)		Metals		Paper/ cardboard packaging		Plastics		Chemical Waste		Others, e.g. rubbish	
	(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in tonne)	
	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW
Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Jun	0.054	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.054	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.600
Sub-total	0.054	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.054	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.600
Jul	0.139	0.000	0.020	0.000	0.000	0.000	0.000	0.000	0.139	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	4.320
Aug	0.345	0.000	0.044	0.000	0.000	0.000	0.000	0.000	0.345	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.930
Sep	1.917	0.029	0.000	0.002	0.000	0.000	0.000	0.000	1.917	0.029	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	4.580
Oct	0.829	0.001	0.000	0.000	0.000	0.000	0.000	0.000	0.829	0.001	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Nov	0.457	0.001	0.003	0.083	0.362	0.000	0.000	0.000	0.095	0.001	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	1.640
Dec	0.780	0.000	0.001	0.019	0.126	0.000	0.000	0.000	0.654	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.390
Total	4.522	0.030	0.068	0.104	0.488	0.000	0.000	0.000	4.033	0.030	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	18.460
	4.552		0.172		0.488		0.000		4.063		0.000		0.000		0.000		0.000		0.000		18.460	

Remark: Assume 1.0 m³ village vehicle dump load = 1.6 tonnes C&D materials

YSW: Yung Shue Wan
SKW: Sok Kwu Wan

Monthly Summary Waste Flow Table for December 2011

Month	Actual Quantities of Inert C&D Materials Generated Monthly												Actual Quantities of C&D Wastes Generated Monthly									
	Total Quantity Generated (a) = (c)+(d)+(e)		Hard Rock and Large Broken Concrete (b)		Reused in the Contract (c)		Reused in other Projects (d)		Disposed as Public Fill (e)		Imported Fill (f)		Metals		Paper/ cardboard packaging		Plastics		Chemical Waste		Others, e.g. rubbish	
	(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in tonne)	
	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW
2010	4.522	0.030	0.068	0.104	0.488	0.000	0.000	0.000	4.033	0.030	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	18.460
Jan	0.985	3.045	0.003	0.013	0.120	0.419	0.000	0.000	0.865	2.626	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	2.240
Feb	0.377	0.000	0.000	0.043	0.000	0.000	0.000	0.000	0.377	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.350
Mar	0.758	1.175	0.002	0.106	0.006	0.000	0.000	0.000	0.752	1.175	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.360
Apr	1.135	1.339	0.017	0.025	0.112	0.180	0.000	0.000	1.023	1.159	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	2.830	5.160
May	0.614	1.362	0.030	0.036	0.014	0.400	0.000	0.000	0.600	0.962	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.150	0.860
Jun	0.505	1.014	0.000	0.022	0.000	0.060	0.000	0.000	0.505	0.954	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	9.610	1.510
Sub-total	8.895	7.965	0.118	0.350	0.740	1.059	0.000	0.000	8.156	6.906	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	15.590	28.940
Jul	0.824	1.077	0.000	0.004	0.000	0.000	0.000	0.000	0.824	1.077	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	5.000	0.510
Aug	0.491	3.519	0.004	0.006	0.000	0.000	0.000	0.000	0.491	3.519	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	7.990	1.830
Sep	0.074	1.473	0.037	0.004	0.000	0.000	0.000	0.000	0.074	1.473	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	23.030	2.420
Oct	0.145	1.674	0.000	0.007	0.000	0.000	0.000	0.000	0.145	1.674	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	16.330	6.850
Nov	0.000	5.176	0.000	0.017	0.000	0.000	0.000	0.000	0.000	5.176	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	81.790	4.590
Dec	0.000	12.659	0.000	0.019	0.000	0.000	0.000	0.000	0.000	12.659	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	57.140	1.550
Total	10.430	33.543	0.160	0.407	0.740	1.059	0.000	0.000	9.690	32.484	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	206.870	46.690
	43.973		0.567		1.799		0.000		42.174		0.000		0.000		0.000		0.000		0.000		253.560	

Remark: Assume 1.0 m³ vehicle dump load = 1.6 tonnes C&D materials

YSW: Yung Shue Wan

SKW: Sok Kwu Wan

Monthly Summary Waste Flow Table for December 2012

Month	Actual Quantities of Inert C&D Materials Generated Monthly												Actual Quantities of C&D Wastes Generated Monthly									
	Total Quantity Generated (a) = (c)+(d)+(e)		Hard Rock and Large Broken Concrete (b)		Reused in the Contract (c)		Reused in other Projects (d)		Disposed as Public Fill (e)		Imported Fill (f)		Metals		Paper/ cardboard packaging		Plastics		Chemical Waste		Others, e.g. rubbish	
	(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in tonne)	
	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW
2012	10.430	33.543	0.160	0.407	0.740	1.059	0.000	0.000	9.690	32.484	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	206.870	46.690
Jan	0.000	3.311	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.311	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	22.530	5.090
Feb	0.170	6.271	0.000	0.000	0.000	0.000	0.000	0.000	0.170	6.271	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	14.860	5.660
Mar	0.619	4.543	0.000	0.000	0.000	0.000	0.000	0.000	0.619	4.543	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	6.940	9.500
Apr	0.157	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.157	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	9.520	1.700
May	0.353	0.916	0.000	0.000	0.000	0.000	0.000	0.000	0.353	0.916	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	6.750	5.090
Jun	0.091	0.000	0.000	0.003	0.000	0.000	0.000	0.000	0.091	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	26.710	6.400
Sub-total	11.820	48.585	0.160	0.410	0.740	1.059	0.000	0.000	11.080	47.526	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	294.180	80.130
Jul	0.248	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.248	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	15.610	2.960
Aug	0.144	0.999	0.000	0.000	0.000	0.999	0.000	0.000	0.144	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	19.730	3.750
Sep	0.686	0.744	0.000	0.000	0.000	0.744	0.000	0.000	0.686	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	26.820	3.800
Oct	0.160	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.160	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	8.970	3.470
Nov	0.131	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.131	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	13.670	4.410
Dec	0.153	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.153	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	21.430	4.920
Total	13.341	50.328	0.160	0.410	0.740	2.802	0.000	0.000	12.601	47.526	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	400.410	103.440
	63.669		0.569		3.542		0.000		60.127		0.000		0.000		0.000		0.000		0.000		503.850	

Remark: Assume 1.0 m³ vehicle dump load = 1.6 tonnes C&D materials

YSW: Yung Shue Wan

SKW: Sok Kwu Wan

Monthly Summary Waste Flow Table for May 2013

Month	Actual Quantities of Inert C&D Materials Generated Monthly												Actual Quantities of C&D Wastes Generated Monthly									
	Total Quantity Generated (a) = (c)+(d)+(e)		Hard Rock and Large Broken Concrete (b)		Reused in the Contract (c)		Reused in other Projects (d)		Disposed as Public Fill (e)		Imported Fill (f)		Metals		Paper/ cardboard packaging		Plastics		Chemical Waste		Others, e.g. rubbish	
	(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000m ³)		(in '000kg)		(in '000kg)		(in '000kg)		(in '000kg)		(in tonne)	
	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW	YSW	SKW
2013	13.341	50.328	0.160	0.410	0.740	2.802	0.000	0.000	12.601	47.526	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	400.410	103.440
Jan	0.332	0.000	0.000	0.005	0.000	0.000	0.000	0.000	0.332	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	9.040	9.840
Feb	0.082	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.082	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	7.530	6.530
Mar	0.056	0.000	0.000	0.003	0.000	0.000	0.000	0.000	0.056	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	10.430	4.920
Apr	0.425	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.425	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	3.800	32.200
May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	1.790	4.650
Jun																						
Sub-total	14.236	50.328	0.160	0.417	0.740	2.802	0.000	0.000	13.497	47.526	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	433.000	161.580
Jul																						
Aug																						
Sep																						
Oct																						
Nov																						
Dec																						
Total	14.236	50.328	0.160	0.417	0.740	2.802	0.000	0.000	13.497	47.526	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	433.000	161.580
	64.564		0.577		3.542		0.000		61.023		0.000		0.000		0.000		0.000		0.000		594.580	

Remark: Assume 1.0 m³ vehicle dump load = 1.6 tonnes C&D materials

YSW: Yung Shue Wan

SKW: Sok Kwu Wan

Appendix K

Weekly Site Inspection Checklist

Project: <u>TCS/00512/09</u> <u>Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan</u>	Inspected by ETL/ ET's Representative: RE's Representative: Contractor's Representative: IEC's Representative:	Checklist No. <u>TCS512A-30 Apr 2013</u> Ms. F. N. Wong Mr. Alfred Cheung/ Kwok Kwai Ming Mr. <i>M.K. Leung</i>
Date: <u>30 April 2013</u>	Time: <u>10:30</u>	Environmental Permit No. <input checked="" type="checkbox"/> EP- 282/2007

PART A: GENERAL INFORMATION

Weather: Sunny Fine Cloudy Rainy

Temperature: °C

Humidity: High Moderate Low

Wind: Strong Breeze Light Calm

Area Inspected
 1 Yung Shue Wan

PART B: SITE AUDIT

Note:	Not Obs.	Yes	No	Follow Up	N/A	Photo/ Remarks
Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable						
Section 1: Water Quality						
1.01 Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02 Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03 Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04 Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05 Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06 Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07 Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08 As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09 Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10 Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11 Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12 Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13 Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14 Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15 Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16 Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17 Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18 Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19 Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20 Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21 Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 2: Air Quality							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 3: Noise							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	


Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 4: Waste/Chemical Management							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
Section 5: Landscape & Visual							
5.01	Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 6: Others							
6.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
6.02	Are the warning sign or larvicidal oil record shown clearly at the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Remarks

Findings of Site Inspection (30 Apr 2013):

- 1) Stagnant water was observed on the roof floor (photos 1 & 2), posing potential of mosquito breeding. Clearance of the stagnant water is required.

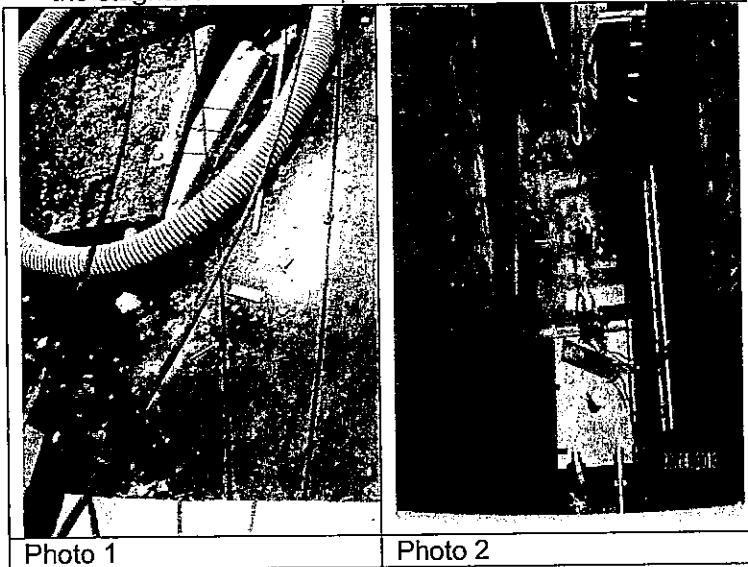

Follow up (7 May 2013):

- 1) Stagnant water on Photo 1 was dried off.
- 2) Mosquito control measures were observed ✓
Wong F. N.
 07 May 2013.

IEC's representative RE's representative ET's representative EO's representative Contractor's representative

(*Alfred Cheung/
Kwok Kwai Ming*)

(*Wong F. N.*)
 07 May 2013

(Mr. *M. K. Leung*)

M. K. Leung

Project: <u>TCS/00512/09</u> <u>Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan</u>	Inspected by ETL/ ET's Representative: RE's Representative: Contractor's Representative: IEC's Representative:	Checklist No. <u>TCS512A-7 May 2013</u> Ms. F. N. Wong Mr. Alfred Cheung/ Kwok Kwai Ming Mr. M. K. Leung _____ _____ _____ _____ _____
Date: <u>7 May 2013</u>	Time: <u>11:30</u>	

PART A: GENERAL INFORMATION

Weather: Sunny Fine Cloudy Rainy

Temperature: °C

Humidity: High Moderate Low

Wind: Strong Breeze Light Calm

Environmental Permit No.
 EP-282/2007

Area Inspected
 1 Yung Shue Wan

PART B: SITE AUDIT

Note:	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
Section 1: Water Quality						
1.01 Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02 Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03 Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04 Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05 Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06 Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07 Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08 As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09 Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10 Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11 Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12 Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13 Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14 Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15 Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16 Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17 Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18 Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19 Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20 Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21 Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 2: Air Quality							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 3: Noise							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 4: Waste/Chemical Management							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
Section 5: Landscape & Visual						
5.01 Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02 Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03 Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04 Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05 Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 6: Others						
6.01 Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
6.02 Are the warning sign or larvicidal oil record shown clearly at the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	


Remarks


Findings of Site Inspection (7 May 2013):


Follow up (07 May 2013): Not required for general reminders.

No adverse environmental impacts were observed. However, full implementation of the required environmental mitigation measures is reminded.

IEC's representative RE's representative ET's representative EO's representative Contractor's representative

()  (Alfred Cheung/
Kwok Kwai Ming)
16 - May - 2013

() (Wong F. N.)
07 May 2013

() (Mr. M. K. Leung) ()

Project: TCS/00512/09 Inspected by _____
 Checklist No. TCS512A-14 May 2013
Construction of Sewage Treatment Works at ETL/ ET's Representative: Ms. F. N. Wong
Yung Shue Wan and Sok Kwu Wan Contractor's Representative: Mr. Alfred Cheung/
 RE's Representative: Kwok Kwai Ming
 Contractor's Representative: Mr. M. K. Leung
 IEC's Representative: _____
 Date: 14 May 2013 Time: 9:30

PART A: GENERAL INFORMATION Environmental Permit No. _____

Weather: Sunny Fine Cloudy Rainy EP- 282/2007

Temperature: °C

Humidity: High Moderate Low

Wind: Strong Breeze Light Calm

Area Inspected
 1 Yung Shue Wan

PART B: SITE AUDIT

Note:	Not Obs.	Yes	No	Follow Up	N/A	Photo/ Remarks
Section 1: Water Quality						
1.01 Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02 Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03 Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04 Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05 Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06 Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07 Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08 As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09 Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10 Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11 Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12 Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13 Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14 Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15 Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16 Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17 Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18 Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19 Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20 Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21 Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 2: Air Quality							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeting?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 3: Noise							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 4: Waste/Chemical Management							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
Section 5: Landscape & Visual							
5.01	Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 6: Others							
6.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
6.02	Are the warning sign or larvicidal oil record shown clearly at the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Remarks

Findings of Site Inspection (14 May 2013):

Follow up (16 May 2013): Not required for general reminders

No adverse impacts were observed. However, full implementation of the required environmental mitigation measures is reminded.

IEC's representative RE's representative ET's representative EO's representative Contractor's representative

() (Alfred Cheung/
Kwok Kwai Ming) (Wong F. N.) (Mr. M. K. Leung) ()

14 May 2013 14 May 2013

Project: TCS/00512/09
Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan

Inspected by
 ETL/ ET's Representative:
 RE's Representative:
 Contractor's Representative:
 IEC's Representative:

Checklist No. TCS512A-21 May 2013
 Ms. F. N. Wong
 Mr. Alfred Cheung/
 Kwok Kwai Ming
 Mr. M. K. Leung

Date: 21 May 2013

Time: 10:30

PART A: GENERAL INFORMATION

Weather: Sunny Fine Cloudy Rainy
 Temperature: 30 °C
 Humidity: High Moderate Low
 Wind: Strong Breeze Light Calm

Environmental Permit No.

EP- 282/2007

Area Inspected
 1 Yung Shue Wan

PART B: SITE AUDIT

Note: Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-Up actions N/A: Not Applicable		Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
Section 1: Water Quality							
1.01	Is an effluent discharge license obtained for the Project?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.02	Is the effluent discharged in accordance with the discharge licence?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.03	Is the discharge of turbid water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.04	Are there proper desilting facilities in the drainage systems to reduce SS levels in effluent?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.05	Are there channels, sandbags or bunds to direct surface run-off to sedimentation tanks?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.06	Are there any perimeter channels provided at site boundaries to intercept storm runoff from crossing the site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.07	Is drainage system well maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.08	As excavation proceeds, are temporary access roads protected by crushed stone or gravel?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.09	Are temporary exposed slopes properly covered?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.10	Are earthworks final surfaces well compacted or protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.11	Are manholes adequately covered or temporarily sealed?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.12	Are there any procedures and equipment for rainstorm protection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.13	Are wheel washing facilities well maintained?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.14	Is runoff from wheel washing facilities avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.15	Are there toilets provided on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.16	Are toilets properly maintained?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.17	Are the vehicle and plant servicing areas paved and located within roofed areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.18	Is the oil/grease leakage or spillage avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.19	Are there any measures to prevent leaked oil from entering the drainage system?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.20	Are there any measures to collect spilt cement and concrete washings during concreting works?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.21	Are there any oil interceptors/grease traps in the drainage systems for vehicle and plant servicing areas, canteen kitchen, etc?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
1.22	Are the oil interceptors/grease traps maintained properly?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.23	Is used bentonite recycled where appropriate?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.24	Designated settlement area for runoff/wheel wash waste is provide and located at the streambed with 1-2m deep, 12m long and around 50m3 capacities for sedimentation.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.25	No excavation is undertaken in the settlement area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.26	Concreting wastes water should be neutralized below the pH Action Levels before discharge.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
1.27	Mobile toilets should provide on site and located away the stream course.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.28	License collector should be employed for handling the sewage of mobile toilet.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
1.29	Is ponding /stand water avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
Section 2: Air Quality							
2.01	Are there wheel washing facilities with high pressure jets provided at every vehicle exit point?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.02	Are vehicles washed to remove any dusty materials from their bodies and wheels before leaving construction sites?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.03	Are the excavated materials sprayed with water during handling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.04	Are stockpiles of dusty materials sprayed with water, covered or placed in sheltered areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.05	Is the exposed earth properly treated within six months after the last construction activities?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.06	Are the access roads sprayed with water to maintain the entire road surface wet or paved?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.07	Is the surface where any drilling, cutting, polishing or breaking operation continuously sprayed with water?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.08	Is the load on vehicles covered entirely by clean impervious sheeling?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.09	Is the loading of materials to a level higher than the side and tail boards during transportation by vehicles avoided?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.10	Is the road leading to the construction site within 30m of the vehicle entrance kept clear of dusty materials?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.11	Is dark smoke emission from plant/equipment avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.12	Are de-bagging, batching and mixing processes carried out in sheltered areas during the use of bagged cement?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.13	Are site vehicles travelling within the speed limit not more than 15km/hour?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
2.14	Are hoardings of not less than 2.4m high provided along the site boundary, which adjoins areas accessible to the public?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.15	Is open burning avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
2.16	Excavated materials from the stream must be removed from the site on the same day. The materials shall be stored in covered impermeable skips awaiting removal from site.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 3: Noise							
3.01	Are noisy equipment and activities positioned as far as practicable from the sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.02	Is silenced equipment adopted?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.03	Is idle equipment turned off or throttled down?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.04	Are all plant and equipment well maintained and in good condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
3.05	Are noise barriers or enclosures provided at areas where construction activities cause noise impact on sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.06	Are hand held breakers fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.07	Are air compressors fitted with valid noise emission labels during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.: Not Observed; Yes: Compliance; No: Non-Compliance; Follow Up: Observations requiring follow-up actions N/A: Not Applicable	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
3.08	Are flaps and panels of mechanical equipment closed during operation?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.09	Are Construction Noise Permit(s) applied for percussive piling works?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.10	Are Construction Noise Permit(s) applied for general construction works during restricted hours?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.11	Are valid Construction Noise Permit(s) posted at site entrances?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.12	Use of quiet plant had been used on site to minimise the construction noise impact to the surrounding residences/dwellings (Level 1 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.13	Temporary/Moveable noise barrier or site hoarding are provide or erect at the site boundary to minimise the noise impact of the closest NSRs or stationary equipments shield by the noise barrier which cannot visible from NSRs (Level 2 mitigation measure)	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
3.14	Temporary/Moveable noise barrier equal to or more than 3m height with 10kg/m2 are provide for noise mitigation measures (Level 2 mitigation measures).	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 4: Waste/Chemical Management							
4.01	Waste Management Plan had been submit to Engineer for approval.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.02	Are receptacles available for general refuse collection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.03	Is general refuse sorting or recycling implemented?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.04	Is general refuse disposed of properly and regularly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.05	Is the Contractor registered as a chemical waste producer?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.06	Are the chemical waste containers and storage area properly labelled?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.07	Are the chemical wastes stored in proper storage areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.08	Is the chemical container or equipment provided with drip tray?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.09	Is the chemical waste storage area used for storage of chemical waste only?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.10	Are incompatible chemical wastes stored in different areas?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.11	Are the chemical wastes disposed of by licensed collectors?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.12	Are trip tickets for chemical wastes disposal available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.13	Are chemical/fuel storage areas bounded?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.14	Are designated areas identified for storage and sorting of construction wastes?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.15	Are construction wastes sorted (inert and non-inert) on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.16	Are construction wastes reused?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.17	Are construction wastes disposed of properly?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.18	Are site hoardings and signboards made of durable materials instead of timber?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.19	Is trip ticket system implemented for the disposal of construction wastes and records available for inspection?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.20	Are appropriate procedures followed if contaminated material exists?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.21	Is relevant license/ permit for disposal of construction waste or excavated materials available for inspection?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
4.22	Site cleanliness and appropriate waste management training had provided for the site workers.	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
4.23	Contaminated sediments will be managed according to WBTC No.12/2000 and EWTB TC(W) No. 34/2002.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	

Note:	Not Obs.	Yes	No	Follow Up	N/A	Photo/Remarks
Section 5: Landscape & Visual						
5.01	Are retained and transplanted trees in health condition?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.02	Are retained and transplanted trees properly protected?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.03	Are surgery works carried out for the damaged trees?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.04	Is damage to trees outside site boundary due to construction activities avoided?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	
5.05	Is the night-time lighting controlled to minimize glare to sensitive receivers?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
Section 6: Others						
6.01	Are relevant Environmental Permits posted at all vehicle site entrances/exits?	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	
6.02	Are the warning sign or larvicidal oil record shown clearly at the construction site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	

Remarks

Findings of Site Inspection (21 May 2013): Follow up (28/5/2013):

- 1) HVS was covered by climbing plant. Removal of the plant is required
- 2) Stagnant water due to heavy rain was observed within the site (on the roof of the Sewage Treatment Plant). Regular clearance is required to avoid mosquito breeding.
- 3) Direct discharge of rainwater from roof was observed. Pretreatment of the rainwater prior to discharge is required.

28/5/2013 Follow-up actions: 1) climbing plant around the HVS was cleared. 2) Stagnant water: mosquito control measure was observed. Clearance was on going. 3) Direct discharge was not observed. Sedimentation tank was used.

IEC's representative RE's representative ET's representative EO's representative Contractor's representative

() (Alfred Cheung / Kwok Kwai Ming) (Wong F. N.) (Mr. M. K. Leung) ()
 28-5-2013 21 May 2013

Appendix L

Implementation Schedule of Mitigation Measures

Implementation Schedule of Air Quality Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.3.18	2.10.2	Adopting the following good site practices and follow the dust control requirements of the Air Pollution Control (Construction Dust) Regulation: <ul style="list-style-type: none"> • Stockpiles of imported material kept on site should be contained within hoardings, dampened and / or covered during dry and windy weather; • Material stockpiled alongside trenches should be covered with tarpaulins whenever works are close to village houses; • Water sprays should be used during the delivery and handling of cement, sands, aggregates and the like. • Any vehicle used for moving sands, aggregates and construction waste should have properly fitting side and tail boards. Materials should not be loaded to a level higher than the side and tail boards, and should be covered by a clean tarpaulin. 	Work site / during construction	All contractors		√		TM- EIAO, APCO, Air Pollution Control (Construction Dust) Regulation
2.10.3	Section 2	1 hour and 24 hour dust monitoring and site audit	Designated air monitoring locations / throughout construction period	Contractor/ Environmental Team		√		EM&A Manual

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Noise Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location/Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.4.16	3.8.2	Implementation of following measures during the sewer construction: <ul style="list-style-type: none"> • Use of quiet PME or method; • Restriction on the number plant (1 item for each type of plant); and • Good Site Practices <ul style="list-style-type: none"> ➤ Only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme. ➤ Mobile plant, if any, should be sited as far away from NSRs as possible. ➤ Machines and plant (such as trucks) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum. ➤ Plant known to emit noise strongly in one direction should, wherever possible, be orientated so that the noise is directed away from the nearby NSRs. ➤ Material stockpiles and other structures should be effectively utilized, wherever practicable, in screening noise from on-site construction activities. 	Work site /during the construction of Sewer.	Contractor		√		EIAO-TM, NCO
2.10.5 to 2.10.9	Section 35	Noise monitoring	Designated noise monitoring locations / throughout construction period	Contractor/ Environmental Team		√		EM&A Manual

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Water Quality Control Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
Construction Phase								
2.5.23	4.12.1	No-dig method using Horizontal Directional Drilling (HDD) would be used for the installation of main portion of outfall pipes	Marine works site / During construction of submarine outfall	Contractor		√		
4.5.38	4.12.3	<p>Dredging Works</p> <p>Implementation of following measures during the dredging works:</p> <ul style="list-style-type: none"> dredging should be undertaken using closed grab dredgers with a maximum total production rate of 55m³/hr; deployment of 2-layer silt curtains with the first layer enclosing the grab and the second layer at around 50m from the dredging area while dredging works are in progress; dredging operation should be undertaken during ebb tide only; all vessels should be sized such that adequate clearance (i.e. minimum clearance of 0.6m) is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; all pipe leakages should be repaired promptly and plant should not be operated with leaking pipes; excess material should be cleaned from the decks and exposed fittings of barges before the vessel is moved; adequate freeboard (i.e. minimum of 200mm) should be maintained on barges to ensure that decks are not washed by wave action; all barges should be fitted with tight fitting seals to their bottom openings to prevent leakage of material; loading of barges should be controlled to prevent splashing of dredged material to the surrounding water, and barges should not be filled to a level which will cause the overflow of materials or polluted water during loading or transportation; and 	Marine works site and at the identified water sensitive receivers/ During construction	Contractor		√		

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
		<ul style="list-style-type: none"> the decks of all vessels should be kept tidy and free of oil or other substances that might be accidentally or otherwise washed overboard. 						
2.5.39	4.12.4	<p><u>Construction Run-off and Drainage</u></p> <p>Implementation of the following site practices outlined in ProPECC PN 1/94 for “Construction Site Drainage”</p> <ul style="list-style-type: none"> Provision of perimeter channels to intercept storm-runoff from outside the site. These should be constructed in advance of site formation works and earthworks. Works programmes should be designed to minimize works areas at any one time, thus minimizing exposed soil areas and reducing the potential for increased siltation and runoff. Sand / silt removal facilities such as sand traps, silt traps and sediment basins should be provided to remove the sand / silt particles from run-off. These facilities should be properly and regularly maintained. These facilities should be carefully planned to ensure that they would be installed at appropriate locations to capture all surface water generated on site. Careful programming of the works to minimise soil excavation works during rainy seasons. Exposed soil surface should be protected by paving or hydroseeding as soon as possible to reduce the potential of soil erosion. Trench excavation should be avoided in the wet season, and if necessary, these should be excavated and backfilled in short sections. Open stockpiles of construction materials on site should be covered with tarpaulin or similar fabric 	Construction works sites	Contractor		√		ProPECC PN 1/94
2.5.39	4.12.5	<p><u>General Construction Activities</u></p> <ul style="list-style-type: none"> Debris and rubbish generated on-site should be collected, handled and disposed of properly to avoid entering the nearby coastal waters and stormwater drains. 	Construction works sites	Contractor		√		

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location (duration /completion of measures)	Implementation Agent	Implementation Stages**			Relevant Legislation and Guidelines
					D	C	O	
		<ul style="list-style-type: none"> All fuel tanks and storage areas should be provided with locks and be sited on sealed areas, within bunds of a capacity equal to 110% of the storage capacity of the largest tank. Open drainage channels and culverts near the works areas should be covered to block the entrance of large debris and refuse. 						
2.5.39	4.12.6	<u>Wastewater Arising from Workforce</u> Portable toilets should be provided by the Contractors, where necessary, to handle sewage from the workforce. The Contractor should also be responsible for waste disposal and maintenance practices.	Construction works sites	Contractor		√		
2.10.10	Section 4	Water quality monitoring	Designated water monitoring locations/ throughout construction period	Contractor		√		EM&A Manual

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Sediment Contamination Mitigation Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
2.9.24	5.2.1	Carrying out Sediment Quality Investigation	Marine works site / prior to construction	DSD	√			WBTC No. 34/2002
2.9.23	5.2.1	Follow the requirement and procedures for dredged mud disposal specified under the WBTC No. 34/2002.	Marine works site / during dredging works	Contractor		√		WBTC No. 34/2002
2.9.23	5.2.2	Implement appropriate dredging methods which have been incorporated into the recommended water quality mitigation measures.	Marine works site, during dredging works	Contractor		√		
2.9.23	5.2.3	During the transportation and disposal of the dredged sediment, the following measures should be taken: <ul style="list-style-type: none"> • Bottom opening of barges should be fitted with tight fitting seals to prevent leakage of material. Excess material should be cleaned from the decks and exposed fittings of barges and hopper dredgers before the vessel is moved. • Monitoring of the barge loading should be conducted to ensure that loss of material does not take place during transportation. Transport barges or vessels should be equipped with automatic self monitoring devices as specified by the DEP. 	Marine works site and at the identified sensitive receivers	Contractor		√		

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Solid Waste Management Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.9.14	6.6.2	<u>Good site practices</u> <ul style="list-style-type: none"> Nomination of an approved person, such as a site manager, to be responsible for implementation of good site practices, arranging for collection and effective disposal to an appropriate facility, of all wastes generated at the site Training (proper waste management and chemical handling procedure) should be provided for site staffs Appropriate measures to minimize windblown litter and dust during transportation of waste by either covering trucks or by transporting wastes in enclosed containers. Provision of sufficient waste disposal points and regular collection for disposal. Separation of chemical wastes for special handling and appropriate treatment at the Chemical Waste Treatment Facility. Regular cleaning and maintenance programme for drainage systems, sumps and oil interceptors. Maintain records of the quantities of wastes generated, recycled and disposed. 	Work sites/During construction	Contractor		√		Waste Disposal Ordinance (Cap.54)
2.9.15	6.2.3	The Contractor will be required to open a billing account under the Construction Waste Disposal Charging Scheme, and to pay for disposal of all construction waste. The construction waste will be sent to a designated reception facility, which in this case will be YSW RTS, where drivers must present a valid chit for disposal of each load.	Work sites/During construction	Contractor		√		Waste disposal (Amendment) Ordinance 2004
2.9.16	6.2.4	Recommendations to achieve waste reduction include: <ul style="list-style-type: none"> segregation and storage of different types of waste in different containers, skips or stockpiles to enhance reuse or recycling of materials and their proper disposal; to encourage collection of aluminium cans by individual collectors, separate labelled bins should be provided to 	Work sites/During construction	Contractor		√		WBTC No. 4/98, 5/98

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
		segregate this waste from other general refuse generated by the work force; <ul style="list-style-type: none"> any unused chemicals or those with remaining functional capacity should be recycled; use of reusable non-timber formwork to reduce the amount of C&D material; prior to disposal of C&D waste, it is recommended that wood, steel and other metals should be separated for re-use and / or recycling to minimise the quantity of waste to be disposed of to landfill; proper storage and site practices to minimise the potential for damage or contamination of construction materials; and plan and stock construction materials carefully to minimise amount of waste generated and avoid unnecessary generation of waste. 						
2.9.18	6.2.5	<u>General Site Wastes</u> <ul style="list-style-type: none"> A collection area for construction site waste should be provided where waste can be stored prior to removal from site An enclosed and covered area for the collection of the waste is recommended to reduce 'wind blow' of light material 	Work sites/During construction	Contractor		√		Public Health and Municipal Services Ordinance (Cap. 132)
2.9.19	6.2.6 and 6.2.7	<u>Chemical Wastes</u> <ul style="list-style-type: none"> After use, chemical waste should be handled according to the Code of Practice on the Package, Labelling and Storage of Chemical Wastes Any unused chemicals or those with remaining functional capacity should be recycled Waste should be properly stored on site within suitably designed containers and should be collected by an approved licensed waste collectors for disposal at the Chemical Waste Treatment Facility or other licenced facility in accordance with the Waste Disposal (Chemical Waste) (General) Regulation under the Waste Disposal Ordance. 	Work sites/During construction	Contractor		√		Waste Disposal (Chemical Waste) (General) Regulation, Code of Practice on the Packaging Labelling and Storage of Chemical Wastes

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
		<ul style="list-style-type: none"> Any service shop and minor maintenance facilities should be located on hard standing within a bunded area, and sumps and oil interceptors should be provided. Maintenance of vehicles and equipment involving activities with potential for leakage and spillage should be undertaken within the designated areas equipped control these discharges 						
2.9.21 and 2.9.22	6.2.8 and 6.2.9	<p><u>Construction and Demolition Material</u></p> <ul style="list-style-type: none"> The C&D waste should be separated on-site into three categories: <ul style="list-style-type: none"> ➤ public fill, the inert portion of the C&D material (e.g. concrete and rubble), which should be re-used on-site or disposed of at a public filling area; ➤ C&D waste for re-use and / or recycling, the non-inert portion of the C&D material, (e.g. steel and other metals, woods, glass and plastic); ➤ C&D waste which cannot be re-used and / or recycled (e.g. wood, glass and plastic) Where possible, inert material should be re-used on-site Where practicable, steel and other metals should be separated for re-use and/or recycling prior to disposal of C&D material 	During all construction phases	Contractors		√		WBTC No. 4/98, 5/98, 21/2002, 25/99, 12/2000

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Ecological Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.10.11 and 2.10.12	7.2 and 7.3	Carry out monitoring of corals before, during and after marine works.	Work sites / during construction phase	Contractor		√		
2.6.45 to 2.6.48	7.6.1	Use horizontal directional drilling to avoid direct disturbance to corals	Marine works site / during dredging works	Contractor		√		
2.6.57 to 2.6.58	4.12.3	Deploying of 2-layer silt curtains with the first layer enclosing the grab and the second layer at around 50m from the dredging area while dredging works are in progress	All work sites / during construction phase	Contractor		√		
2.6.51	7.6.1	Fence off the slope stabilisation works area from surrounding shrubland and/ woodland, to prevent access to or disturbance of adjacent habitats. The works area should be as small as is possible, consistent with the requirements of the works.	STW/ During construction	Contractor		√		

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Implementation Schedule of Fisheries Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages**			Relevant Legislation & Guidelines
					D	C	O	
2.5.37	4.12.4	Use of closed grab dredging and silt curtains around the immediate dredging area and low dredging rates as recommended in Water Quality of the EIA report	Marine works site, during dredging works	Contractor		√		TM on EIA Process

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.
 ** D=Design, C=Construction, O=Operation
 N/A Not applicable

Implementation Schedule of Landscape and Visual Impact Measures

EIA Ref	EM&A Ref	Environmental Protection Measures*	Location / Timing	Implementation Agent	Implementation Stages **			Relevant Legislation & Guidelines
					D	C	O	
Construction Phase								
2.8.37	9.2.2	Careful and efficient transplanting of affected trees to temporary or final transplant location (the proposed tree to be transplanted is a semi-mature <i>Macaranga tanarius</i> and is located at the proposed Pumping Station P2 location).	All sites	Contractor		√		WBTC No. 14/2002
2.8.37	9.2.2	Short excavation and immediate backfilling sections upon completion of works to reduce active site area.	All sites	Contractor		√		
2.8.37	9.2.2	Screening of site construction works by use of hoarding that is appropriate to its site.	All sites	Contractor		√		WBTC No. 19/2001
2.8.37	9.2.2	Conservation of topsoil for reuse.	All sites	Contractor		√		
2.8.30	9.2.2	Night-time light source from marine fleets should be directed away from the residential units.	Outfall area.	Contractor		√		

* All recommendations and requirements resulted during the course of EIA Process, including ACE and/or accepted public comment to the proposed project.

** D=Design, C=Construction, O=Operation

N/A Not applicable

Appendix M

Corresponding Letter



Our Ref.: 1004/28.02.03.00/7344/T.
Date: 18 June 2013

Action-United Environmental Services & Consulting
Flat A, 20/F, Gold King Industrial Building,
35-41, Tai Lin Pai Road,
Kwai Chung, N.T.
Hong Kong

By Fax & By Post
(Fax No.2959 6079)

Attn: Mr. TW Tam/ Ms Nicola Hon

Dear Madam,

Drainage Services Department
Contract No. DC/2009/13
Construction of Sewage Treatment Works at Yung Shue Wan and Sok Kwu Wan
Completion of Marine Works in Yung Shue Wan

Please be informed that all marine based construction activities, including Horizontal Directional Drilling works, submarine outfall pipe installation, dredging works, diffuser installation and backfilling works in Yung Shue Wan have been completed on 23 April 2013.

Should you have any queries, please feel free to contact our Mr. Ron Hung at 2982 1750 or by fax at 2982 1803.

Thank you for your kind attention.

Yours faithfully,
For and on behalf of
Leader Civil Engineering Corporation Limited

Vincent Chan
Site Agent

VC/RH/te

c.c. URS CDM JV

Attn: Mr. Ian Jones

(By Hand)

Leader Civil Engineering Corporation Ltd.

Units 601-605A, 6/F., Tower B, Manulife Financial Centre, 223 Wai Yip Street, Kwun Tong, Kowloon, Hong Kong Tel: (852) 2272 3680 Fax: (852) 2375 3655

利達土木工程有限公司 香港九龍官塘偉業街223號宏利金融中心B座六樓601至605A室 電話: (852) 2272 3680 傳真: (852) 2375 3655

A MEMBER OF BUILD KING GROUP 利達控股集團成員
